

PROJECT No.: TCS/00553/11

CONTRACT NO. DC/2010/02 –
DRAINAGE IMPROVEMENT IN SHUEN WAN AND SHEK WU WAI

MONTHLY ENVIRONMENTAL MONITORING AND AUDIT REPORT (NO.22) – APRIL 2013

PREPARED FOR KWAN LEE-KULY JOINT VENTURE

Quality Index

Date Reference No. Prepared By Certified by

21 May 2013 TCS00553/11/600/R0261v2

Nicola Hon T.W. Tam
(Environmental Consultant) (Environmental Team Leader)

Ver.	Date	Description
1	20 May 2013	First submission
2	21 May 2013	Amended against IEC's comments on 21 May 2013

This report has been prepared by Action-United Environmental Services & Consulting with all reasonable skill, care and diligence within the terms of the Agreement with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies upon the report at their own risk.



Ref.: DSDSHUWNEM00_0_0576L.12

23 May 2013

Drainage Services Department Drainage Projects Division 44 & 45/F., Revenue Tower 5 Gloucester Road, Wan Chai, Hong Kong By Fax (2827 8700) and Post

Attention: Mr. H.K.Chan and Mr. So Chi Ho

Dear Sirs,

Re: Agreement No. DP 01/2010

Services as Independent Environmental Checker for the Drainage Improvement Works in Sha Tin and Tai Po under Contract No. DC/2010/02

Monthly Environmental Monitoring and Audit Report for Apr 2013

Reference is made to Environment Team's submission of the Monthly Environmental Monitoring and Audit Report for Apr 2013 by Email on 20 May 2013 (entitled "DC/2010/22 - Monthly Impact EM&A Report (Contract 2) No.22 - Apr 2013").

Please be informed that we have no comment on the captioned revised report. We write to verify the captioned submission in accordance with Condition 5.4 of EP-303/2008.

Thank you very much for your kind attention and please do not hesitate to contact Mr. Max Lee (3465 - 2809) or the undersigned should you have any queries.

Yours sincerely,

Tony Cheng

Independent Environmental Checker

c.c. AUES Kwan Lee-Kuly JV Attn: Mr. T. W. Tam Attn: Mr. W. K. Chan By Fax: 2959 6079 By Fax: 2674 6688

Q:\Projects\DSDSHUWNEM00\Corr\Out\DSDSHUWNEM00 0 0576L.12.doc



EXECUTIVE SUMMARY

ES.01. This is the 22nd Monthly Environmental Monitoring and Audit (EM&A) Report for designated works of *DSD Contract No. DC/2010/02 - Drainage Improvement in Shuen Wan and Shek Wu Wai* (hereafter "Contract 2") under Environmental Permit No.EP-303/2008, covering a period from 1 to 30 April 2013 (hereinafter 'the Reporting Period').

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES.02. Environmental monitoring activities under the EM&A programme in this Reporting Period are summarized in the following table.

Issues	Environmental Monitoring Parameters / Inspection	Occasions
Construction	Construction L _{eq (30min)} Daytime – M2, M3 & M4	
Noise	Noise $L_{eq (30min)}$ Daytime – M1 & AL1	
	Local Stream Water Sampling - W1, W3 and W4	12
Water Ovality	Local Stream Water Sampling – W2	12
Water Quality	Hydrological characteristics measurement – H1 and H2	4
	Hydrological characteristics measurement – H3 and H4	4
Inspection /	Monthly Environmental Site Inspection and audit by IEC	1
Audit	Regular weekly Environmental inspection by the Contractor, ET and Site Representative Engineer	4
Ecological Bi- monthly Ecological Monitoring		0
Landscape & Visual Bi-weekly Inspection by a registered Landscape Architect		3

- ES.03. In this Reporting Period, no bi-monthly ecological monitoring in Area under Contract 2 was performed.
- ES.04. Landscape and visual inspection was carried on 5, 18 and 30 April 2013 and the monthly Landscape & Visual Report (April 2013) has been signed by the registered Landscape Architect.

BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES.05. No exceedance in construction noise monitoring is recorded in this Reporting Period. For water quality monitoring, a total of 103 Action/ Limit Level exceedances, namely 39 exceedances in dissolved oxygen, 37 exceedances in turbidity and 27 exceedances in suspended solids were recorded in this Reporting Period. NOEs were issued to notify EPD, IEC, the Contractor and RE upon confirmation of the results. The statistics of environmental exceedance, NOE issued and investigation result are summarized in the following table.

Environmental	Monitoring	Action	Limit Level	Event & Action		
Issues	Parameters Parameters			NOE Issued	Investigation	Corrective Actions
Construction Noise	$L_{eq(30min)}$ Daytime	0	0	0	N.A.	N.A.
	DO	39	0	39	Exceedances at	
W 4 0 114	Turbidity	7	30	37	W4 were	Cover all exposed
Water Quality	SS		24	27	partially due to works under project	slope to prevent surface runoff
Hydrological	Water Flow	0	0	0	N.A.	N.A.
Characteristics	Water Depth	0	0	0	N.A.	N.A.

Note: NOE – Notification of Exceedance

SITE INSPECTION

ES.06. Weekly environmental site inspections had been carried out by the Contractor, ET and the RE on 3, 10, 17 and 26 April 2013. Furthermore, joint site inspection with the IEC was carried out on



26 April 2013. In this Reporting Period, **4** observations were recorded but no non-compliance was noted during the site inspection.

ENVIRONMENTAL COMPLAINT

ES.07. No written or verbal complaint was recorded in this Reporting Period.

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES.08. No environmental summons or successful prosecutions were recorded in this Reporting Period.

REPORTING CHANGE

ES.09. No report changes were made in this Reporting Period.

FUTURE KEY ISSUES

- ES.10. During wet season, muddy water and other water quality pollutants via site surface water runoff into the local stream Wah Ha River would be the key issue in the forth-coming month. Mitigation measures for water quality should be fully implemented.
- ES.11. On the other hand, construction noise should be other key environmental issue during sheet-piling process. The noise mitigation measures should be necessary to implement in accordance with EM&A Manual stipulation. Dust mitigation measures to avoid fugitive dust emissions from loose soil surface or haul road is also reminded.

 $DSD\ Contract\ No.\ Contract\ No.\ DC/2010/02$ - Drainage Improvement in Shuen Wan and Shek Wu Wai





TABLE OF CONTENTS

1.0	INTRODUCTION		1
	PROJECT BACKGROUND	1	
	REPORT STRUCTURE	1	
2.0	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS AND SUBMISSION		2
	PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE	2	
	CONSTRUCTION PROGRESS	2	
	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	2	
3.0	EM&A PROGRAM REQUIREMENT FOR THE CONTRACT 2		3
	MONITORING PARAMETERS	3	
	MONITORING LOCATIONS	3	
	MONITORING FREQUENCY	4	
	MONITORING EQUIPMENT	5	
	MONITORING METHODOLOGY	6	
	DATA MANAGEMENT AND DATA QA/QC CONTROL	8	
	OTHERS MONITORING IMPLEMENTATION FOR THE CONTRACT	8	
	DETERMINATION OF ACTION/LIMIT (A/L) LEVELS	8	
	EQUIPMENT CALIBRATION	9	
	METEOROLOGICAL INFORMATION	9	
4.0	IMPACT MONITORING RESULTS		10
	MONITORING RESULTS SHARING	10	1
	RESULTS OF CONSTRUCTION NOISE MONITORING	10	1
	RESULTS OF LOCAL STREAM WATER QUALITY MONITORING	10	1
	RESULTS OF HYDROLOGICAL CHARACTERISTICS MONITORING	12	
	RESULTS OF ECOLOGICAL MONITORING	13	
5.0	WASTE MANAGEMENT		14
	RECORDS OF WASTE QUANTITIES	14	
6.0	SITE INSPECTION		15
	REGULAR SITE INSPECTION AND MONTHLY AUDIT	15	
	LANDSCAPE AND VISUAL INSPECTION	15	
7.0	ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE		16
	ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	16	
8.0	IMPLEMENTATION STATUS OF MITIGATION MEASURES		17
9.0	IMPACT FORCAST		21
	CONSTRUCTION ACTIVITIES FOR THE FORTH-COMING MONTH	21	
	KEY ISSUES FOR THE COMING MONTH	21	
10.0	CONCLUSIONS AND RECOMMENTATIONS		22
	CONCLUSIONS	22	,
	RECOMMENDATIONS	22	,



LIST OF TABLES

ΓABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS
TABLE 3-1	SUMMARY OF MONITORING PARAMETERS
ΓABLE 3-2	DESIGNATED MONITORING LOCATIONS OF THE EM&A PROGRAMME
TABLE 3-3	MONITORING EQUIPMENT USED IN EM&A PROGRAM
ΓABLE 3-4	TESTING METHOD AND DETECTION LIMIT OF SUSPENDED SOLIDS
TABLE 3-5	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
ΓABLE 3-6	ACTION AND LIMIT LEVELS FOR WATER QUALITY
ΓABLE 3-7	ACTION AND LIMIT LEVELS FOR HYDROLOGICAL CHARACTERISTICS
ΓABLE 4-1	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS, dB(A)
ΓABLE 4-2	WATER QUALITY RESULTS SUMMARY FOR W1 & W2
ΓABLE 4-3	WATER QUALITY RESULTS SUMMARY FOR W3 & W4
ΓABLE 4-4	STATISTICS WATER QUALITY EXCEEDANCE IN THE REPORTING PERIOD
ΓABLE 4-5	DETAILED MONITORING RESULTS OF HYDROLOGICAL CHARACTERISTICS AT H3 AND H4
ΓABLE 4-6	SUMMARIZED HYDROLOGICAL CHARACTERISTICS OF WATER DEPTH, M
ΓABLE 4-7	SUMMARIZED HYDROLOGICAL CHARACTERISTICS OF AVERAGE VOLUMETRIC FLOW RATE
	$(Q), M^3/S$
ΓABLE 5-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
ΓABLE 5-2	SUMMARY OF QUANTITIES OF C&D WASTES
ΓABLE 6-1	SITE INSPECTION OF OBSERVATIONS – FINDINGS AND DEFICIENCIES
ΓABLE 6-2	LANDSCAPE & VISUAL INSPECTION OF OBSERVATIONS
ΓABLE 7-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
ΓABLE 7-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
ΓABLE 7-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
Table 8-1	ENVIRONMENTAL MITIGATION MEASURES

LIST OF APPENDICES

APPENDIX A APPENDIX B	SITE LOCATION PLAN OF DSD CONTRACT 1 AND CONTRACT 2 AT SHUEN WAN ORGANIZATION CHART AND THE KEY CONTACT PERSON		
APPENDIX C	MASTER CONSTRUCTION PROGRAMS		
APPENDIX D	ENVIRONMENTAL MONITORING LOCATIONS		
APPENDIX E	CALIBRATION CERTIFICATES OF THE MONITORING EQUIPMENT AND CERTIFICATE OF ALS		
	TECHNICHEM (HK) PTY LTD		
APPENDIX F	EVENT AND ACTION PLAN		
APPENDIX G	MONITORING SCHEDULE IN REPORTING PERIOD AND COMING MONTH		
APPENDIX H	METEOROLOGICAL DATA OF REPORTING PERIOD		
APPENDIX I	DATA BASE OF MONITORING RESULT S		
APPENDIX J	GRAPHICAL PLOTS OF IMPACT MONITORING -NOISE, WATER QUALITY AND		
	HYDROLOGICAL CHARACTERISTICS		
APPENDIX K	MONTHLY SUMMARY WASTE FLOW TABLE		
APPENDIX L	MONTHLY LANDSCAPE & VISUAL INSPECTION REPORT		
APPENDIX M	ECOLOGICAL MONITORING REPORT IN AREA UNDER CONTRACT 2 (NOT USED)		



1.0 INTRODUCTION

PROJECT BACKGROUND

- 1.01 *Kwan Lee-Kuly Joint Venture* (hereinafter 'KLKJV') has been awarded by Drainage Services Department (hereinafter 'DSD') of the Contract No. DC/2010/02 Drainage Improvement in Shuen Wan and Shek Wu Wai (hereinafter 'the Project'). The Project is scheduled to commence in May 2011 and complete in March 2014 for about 35 months.
- 1.02 The works to be executed under the Project are located in Shuen Wan and Shek Wu Wai. The works mainly comprise construction of about 735 metres long single-cell box culvert along Tung Tsz Road in Shuen Wan, Tai Po and construction of about 15 m long three-cell box culvert in Shek Wu Wai, San Tin.
- 1.03 For the Project, the construction work at Tung Tsz Road Shuen Wan (hereinafter 'the Contract 2') is part of the Drainage Improvement works amongst Shatin and Tai Po and it is defined as a "Designated Project" which controlled under Environmental Permit EP-303/2008. Currently, DSD has another Contract DC/2009/22 (hereinafter 'the Contract 1') ongoing for construction at Shuen Wan working area which under the same Environmental Permit and the updated Environmental Monitoring and Audit Manual (hereinafter 'the Updated EM&A Manual'). Both DSD contract's site boundary at Shuen Wan are shown in *Appendix A*. On the other hand, Shek Wu Wai San Tin is a non-designated project work and no environmental monitoring and audit is request to carry out.
- 1.04 In order to effectively implement the environmental protection measures stipulated in the Project Profile (hereinafter 'the PP'), Environmental Impact Assessment Report (hereinafter "the EIAR'), Environmental Permit EP303/2008, a corresponding EM&A Manual have been prepared to outline the environmental monitoring and auditing (hereinafter 'the EM&A') programme undertake for the Contracts 1 and 2.
- 1.05 KLKJV has commissioned Action-United Environmental Services and Consulting (AUES) as an independent environmental team (hereinafter 'the ET') to implement the EM&A program for the environmental protection of the Project. Due to the construction of Contracts 1 and 2 carry out is just about the time, a Proposal Environmental Monitoring Programme and Methodology (hereinafter the "PEMPM") was prepared and submitted to describe EM&A programme would be undertaken during construction period of the Contract 2.
- 1.06 The baseline monitoring of EM&A program has been performed by the Contract 1 ET. Although Action and Limit levels of environmental performance criteria have established by the Contract 1 ET, the Action/Limit levels re-establishment to use the Contract 2 was conducted by the Contract 2 ET. The re-established environment performance criteria has accepted by the IEC and also submitted to the EPD seek for endorsement.
- 1.07 This is the 22nd Monthly EM&A Report for Contract 2 presenting the monitoring results and inspection findings for the reporting period from 1 to 30 April 2013.

REPORT STRUCTURE

- 1.08 The Monthly Environmental Monitoring and Audit (EM&A) Report is structured into the following sections:-.
 - SECTION 1 INTRODUCTION
 - SECTION 2 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS AND SUBMISSION
 - SECTION 3 EM&A PROGRAM REQUIREMENT FOR THE PROJECT
 - SECTION 4 IMPACT MONITORING RESULTS
 - SECTION 5 WASTE MANAGEMENT
 - SECTION 6 SITE INSPECTIONS
 - SECTION 7 ENVIRONMENTAL COMPLAINTS AND NON-COMPLIANCE
 - SECTION 8 IMPLEMENTATION STATUES OF MITIGATION MEASURES
 - SECTION 9 IMPACT FORECAST
 - SECTION 10 CONCLUSIONS AND RECOMMENDATION



2.0 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS AND SUBMISSION

PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE

2.01 Organization structure and contact details of relevant parties with respect to on-site environmental management are shown in *Appendix B*.

CONSTRUCTION PROGRESS

2.02 The master construction programs are enclosed in *Appendix C* and the major construction activities undertaken at Tung Tsz Road, Shuen Wan in this Report Period are listed below:-

Tung Tze Road

- Fixing steel reinforcement at bay 45
- Erection of formwork at bay 44, 45
- Removal of formwork at bay 44, 45, 46
- Backfilling at bay 43 46
- Removal of sheetpile at bay 43, 44, 46, 47
- Construction of intake structure, Water Diversion Water

Wai Ha Road

- Laying geotextile and rockfill at bay 10
- Concreting blinding layer at bay 10
- Fixing steel reinforcement at bay 10
- Erection of formwork at bay 9

SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.03 Summary of the relevant permits, licences, and/or notifications on environmental protection for this Project in this Reporting Period is presented in *Table 2-1*.

Table 2-1 Status of Environmental Licenses and Permits

Item	Description	License/Permit Status
1	Air Pollution Control (Construction Dust)	Notified EPD on 17 October 2011
2	Chemical Waste Producer Registration (WPN5213-727-K2972-02)	Approved on 28 October 2011
3	Water Pollution Control Ordinance (Discharge License) WT00009528-2011	Valid to 31 July 2016
4	Billing Account for Disposal of Construction Waste (Account No.: 7012838)	Effective

- 2.04 The "Proposal Environmental Monitoring Programme and Methodology (R0006 Version 2)" was set out in accordance with the Updated Environmental Monitoring and Audit Manual. It was approved by the ER and agreed with the Independent Environmental Checker (IEC) and submitted to the EPD for endorsement.
- 2.05 For Contract 2 of the Project, no Baseline Monitoring Report was issued by the ETL. However, a new set of the Action/ Limit levels as used to Contract 2 were proposed by ET. It had been accepted by the IEC and also submitted to the EPD seek for endorsement.



3.0 EM&A PROGRAM REQUIREMENT FOR THE CONTRACT 2

3.01 The EM&A requirements set out in the PP, EIAR, Environmental Permit EP303/2008 (hereinafter 'the EP'), and the associated updated EM&A Manual, are presented below sub-section.

MONITORING PARAMETERS

3.02 According to the EIAR and the updated EM&A Manual, The monitoring parameters of each environmental aspect summarized in *Table 3-1* will be performed as under the Project.

Table 3-1 Summary of Monitoring Parameters

Environmental Aspect	Parameters		
Construction Noise	 A-weighted equivalent continuous sound pressure level (30min) (hereinafter 'Leq(30min)' during the normal working hours; and A-weighted equivalent continuous sound pressure level (5min) (hereinafter 'Leq(5min)' for construction work during the restricted hours. 		
Water Quality	In Situ Measurement Laboratory Analysis	Temperature, Dissolved Oxygen, Dissolved Oxygen Saturation, pH and Turbidity Suspended Solids (hereinafter 'SS')	
Hydrological Characteristics			
*Ecology	Monitor and audit the proper implementation of mitigation measures stipulated in EIA report and the updated EM&A Manual		
Landscape & Visual	Inspect and audit the implementation and maintenance of landscape and visual mitigation measures		

Remarks: * the monitoring is carried out by IEC

MONITORING LOCATIONS

3.03 Monitoring locations have been proposed in the updated EM&A Manual. Graphic plot to show in *Appendix D* and summarized in *Table 3-2*.

Table 3-2 Designated Monitoring Locations of the EM&A Programme

Aspect	Location ID	Address
	M1	14, Shuen Wan Chim Uk
Construction	AL1	Joint Village Office for Villages in Shuen Wan, Tai PO
Noise	M2	150, San Tau Kok
Noise	M3	31, Wai Ha
	M4	Block 15, T rèasure Spot Garden
		Between the Shuen Wan Marsh and ECA
	^(#) W1	• Co-ordinates: E839301, N836386
		• Existing River Bed Level: +1.75mPD).
	W2	Between Tolo Harbour and Proposed Penstock
		• Co-ordinates: E839542, N836184
Water Quality		• Exiting River Bed Level: +1.48mPD)
water Quarity	(*) W3	Upstream of Tung Tze Shan Road
		• Co-ordinates: E838760, N836714
		• Exiting River Bed Level: +5.08mPD)
	W4	Wai Ha Village 29D
		• Co-ordinates: E838865, N836621
		• Exiting River Bed Level: +4.05mPD)
	H1	Between the Shuen Wan Marsh and ECA
Hydrological		• Coordinates: E839306, N836379)
Trydrological	H2	Route 10 Sam Kung Temple
		• Coordinates: E839163, N836433



Aspect	Location ID	Address	
112		Upstream of Tung Tze Shan Road	
	Н3	• Coordinates: E838760, N836714	
	114	Wai Ha Village 29D	
	H4	• Coordinates: E838865, N836621	
Ecology	Areas within 100m of the works boundary under Contract 2		
Landscape &	cape & As within and adjacent to the construction sites and works areas under the Con		
Visual	2,		

Remarks:

MONITORING FREQUENCY

3.04 The monitoring frequency and duration as specified in the updated EM&A Manual are summarized below.

Construction Noise

Frequency: Once a week during 0700-1900 on normal weekdays for L_{eq(30min)}

If the construction work is undertake at restricted hour, the monitoring frequency of construction noise will be conducted in accordance with the related Construction Noise Permit requirement issued by EPD as follow

- 3 consecutive L_{eq(5min)} at restrict hour from 1700 − 2300;
- 3 consecutive $L_{eq(5min)}$ for restrict hour from 2300 0700 next day;
- 3 consecutive L_{eq(5min)} for Sunday or public holiday from 0700 1900;

<u>Duration</u>: Throughout the construction period when the major construction activities are undertaken

Water Quality

Frequency: Three times a week. The interval between 2 sets monitoring are not less than 36

hours

Duration: During the construction phase of Contract 2 to undertake (in accordance with the

Updated EM&A Manual Section 4.27).

Hydrological Characteristics

Frequency: Once per week at mid-flood and mid-ebb tides

<u>Duration</u>: During the construction phase of Contract 2 to undertake; and one year after the

construction is complete as operation phase monitoring (in accordance with the

Updated EM&A Manual Section 4.32).

Ecology

3.05 In according with Section 6.17 of the Updated EM&A Manual, ecological monitoring should be conducted by the Independent Environmental Checker (hereinafter 'IEC'). Monitoring programme details should be agreed with the Agriculture, Fisheries and Conservation Department (AFCD). Moreover, the IEC should submit reports on the findings of each monitoring trip, and a final report summarizing the monitoring results over the entire monitoring period to AFCD and Environmental Protection Department (EPD). Hence, no monitoring or surveying should be carried out by ET of the Project.

Landscape & Visual

3.06 According to Section 7.4 of the Updated EM&A Manual, site inspection bi-weekly should be performed to check the implementation and maintenance of landscape and visual mitigation measures whether to full realize.

^(#) Control Station of Contract 1, however impact station of Contract 2

^(*) Control Station of Contract 2



MONITORING EQUIPMENT

Noise Monitoring

3.07 Sound level meter in compliance with the *International Electrotechnical Commission Publications* 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for noise monitoring. The sound level meter shall be checked with an acoustic calibrator. The wind speed shall be check with a portable wind speed meter, which capable to measure wind speed in m/s.

Water Quality Monitoring

- 3.08 **Dissolved Oxygen and Temperature Measuring Equipment** The instrument should be a portable and weatherproof dissolved oxygen (DO) measuring instrument complete with cable and sensor, and use a DC power source. The equipment should be capable of measuring DO level in the range of 0 20mg L-1 and 0 200% saturation; and temperature of 0 45 degree Celsius.
- 3.09 **pH Meter** The instrument shall consist of a potentiometer, a glass electrode, a reference electrode and a temperature-compensating device. It shall be readable to 0.1 pH in arrange of 0 to 14.
- 3.10 **Turbidity (NTU) Measuring Equipment** The instrument should be a portable and weatherproof turbidity measuring instrument using a DC power source. It should have a photoelectric sensor capable of measuring turbidity between 0 1000 NTU.
- 3.11 **Water Sampling Equipment** A water sampler should comprise a transparent PVC cylinder, with a capacity of not less than 2 litres, which can be effectively sealed with latex cups at both ends. The sampler should have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth.
- 3.12 **Water Depth Detector** A portable, battery-operated echo sounder should be used for the determination of water depth at each designated monitoring station. The unit can either be hand held or affixed to the bottom of the work boat.
- 3.13 **Sample Containers and Storage** Water samples for SS should be stored in high density polythene bottles with no preservative added, packed in ice (cooled to 4°C without being frozen).
- 3.14 **Suspended Solids Analysis** Analysis of suspended solids shall be carried out in a HOKLAS or other international accredited laboratory.

Hydrological Characteristics

- 3.15 **Water Depth Detector** A portable, battery-operated echo sounder shall be used for the determination of water depth at each designated monitoring station.
- 3.16 **Stream water flow Equipment** –A portable, battery-operated flow meter should be used for the determination of water flow rate at each designated monitoring location and record in m³/s.
- 3.17 The monitoring equipment using for the Project's EM&A program were proposed by the ET and verified by the IEC prior commencement of the monitoring. Details of the equipment used for impact monitoring are listed in *Table 3-3*.

Table 3-3 Monitoring Equipment Used in EM&A Program

Equipment	Model
Construction Noise	
Integrating Sound Level Meter	B&K Type 2238
Calibrator	B&K Type 4231
Portable Wind Speed Indicator	Testo Anemometer
Water quality	
Water Depth Detector	Eagle Sonar
Water Sampler	A transparent PVC cylinder / bucket



Equipment	Model
Thermometer & DO meter	YSI DO Meter 550A or YSI Professional Plus or YSI Sonde6820 / 650MDS
pH meter	YSI pH10N or YSI Professional Plus or YSI Sonde 6820 / 650MDS
Turbidimeter	Hach 2100Q or YSI Sonde 6820 / 650MDS
Sample Container	High density polythene bottles (provided by laboratory)
Storage Container	'Willow' 33-litre plastic cool box
Suspended Solids	HOKLAS-accredited laboratory (ALS Technichem (HK) Pty
Suspended Sonds	Ltd)
Hydrological Characteristics	
Water flow meter	GLOBAL WATER model FP211
Water Depth Detector	Eagle Sonar or an appropriate steel ruler or rope with
water Depth Detector	appropriate weight

MONITORING METHODOLOGY

Noise Monitoring

- 3.18 Noise measurements were taken in terms of the A-weighted equivalent sound pressure level (L_{eq}) measured in decibels (dB). Supplementary statistical results (L_{10} and L_{90}) were also obtained for reference.
- 3.19 Sound level meter as listed in *Table 3-3* are complied with the *International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1)* specifications, as recommended in Technical Memorandum (TM) issued under the *Noise Control Ordinance (NCO)*.
- 3.20 During the monitoring, all noise measurements were performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (L_{eq}). $Leq_{(30min)}$ in six consecutive $Leq_{(5min)}$ measurements were used as the monitoring parameter for the time period between 0700-1900 hours on weekdays; and also $Leq_{(15min)}$ in three consecutive $Leq_{(5min)}$ measurements is used as monitoring parameter for other time periods (e.g. during restricted hours), if necessary.
- 3.21 During the course of measurement, the sound level meter is mounted on a tripod with a height of 1.2m above ground and placed at the assessment point and oriented such that the microphone is pointed to the site with the microphone facing perpendicular to the line of sight. The windshield is fitted for all measurements. The assessment point is normally set as free-field situation for the measurement.
- 3.22 Prior to noise measurement, the accuracy of the sound level meter is checked by an acoustic calibrator which generated a known sound pressure level at a known frequency. The checking was performed before and after the noise measurement.

Water Quality

- 3.23 Water quality monitoring are conducted at the depth below:-
 - Three depths: 1m below water surface, 1m above river bed and at mid-depth when the water depth exceeds 6m, or
 - If the water depth is between 3m and 6m, two depths: 1m below water surface and 1m above river bed, and or
 - If the water depth is less than 3m, 1 sample at mid-depth is taken
- 3.24 Water depths are determined prior to measurement and sampling, using a portable battery operated depth detector, brand named 'Eagle Sonar', if the depths exceed 1.5 meter. If the depth between 1.5 meter and 1 meter, plastic tape measurement tied with appropriate weight are used the depth estimation. For the depth well below 1 meter, an appropriate steel ruler or rope with appropriate weight are used for the depth measurement.



- 3.25 A transparent PVC cylinder, with a capacity of not less than 2 litres, is used for water sampling. The water sampler is lowered into the water body at a predetermined depth. The trigger system of the sampler is activated with a messenger and opening ends of the sampler are closed accordingly then the sample of water is collected. If the water depth is less than 500mm, a water bucket is be used as a water sampler to minimize the possibility of the latching system disturbing sediment during water sampling
- 3.26 A portable YSI DO Meter 550A or YSI Professional Plus is used for in-situ DO measurement. The DO meter is capable of measuring DO in the range of 0 20 mg/L and 0 200 % saturation and checked against water saturated ambient air on each monitoring day prior to monitoring. Although the DO Meter automatically compensates ambient water temperature to a standard temperature of 20°C for ease of comparison of the data under the changing reality, the temperature readings of the DO Meter are be recorded in the field data sheets. The equipment calibration is performed on quarterly basis.
- 3.27 A portable YSI pH10N Meter or or YSI Professional Plus is used for in-situ pH measurement. The pH meter is capable of measuring pH in the range of 0 14 and readable to 0.1. Standard buffer solutions of pH 7 and pH 10 are used for calibration of the instrument before and after measurement. The equipment calibration is performed on quarterly basis.
- 3.28 A portable Hach 2100Q Turbidity Meter is be used for in-situ turbidity measurement. The turbidity meter is capable of measuring turbidity in the range of 0-1000 NTU. The equipment calibration is performed on quarterly basis.
- 3.29 Water samples are contained in screw-cap PE (Poly-Ethylene) bottles, which are provided and pretreated and 'PE' (Poly-Ethylene) sampling bottles provided and pre-treated according to corresponding analytical requirements. Where appropriate, the sampling bottles are rinsed with the water to be contained. Water sample is then transferred from the sampler to the sample bottles.
- 3.30 One liter or 500 mL water sample are collected from each depth for SS determination. The collected samples are stored in a cool box maintained at 4°C and delivered to laboratory upon completion of the sampling by end of each sampling day.
- 3.31 All water samples are analyzed with Suspended Solids (SS) as specified in the updated *EM&A Manual* by a local HOKLAS-accredited testing laboratory (ALS Technichem (HK) Pty Ltd HOKLAS registration no. 66). SS are determined by the laboratory upon receipt of the water samples using HOKLAS accredited analytical method. The detection limits and testing method are shown below in *Table 3-4*. The certificate of ALS Technichem (HK) Pty Ltd is provided in *Appendix E*.

Table 3-4 Testing Method and Detection limit of Suspended Solids

Determinant	Testing Method	Detection Limit
Suspended solid	Determination use HOKLAS accredited analytical methods namely ALS Method EA-025 (based on APHA 2540 D)	2mg/L

Hydrological Characteristics

- 3.32 A portable, water flow meter, brand named "GLOBAL WATER model FP211" are used to determine the water current flow at the designated monitoring stations. A water flow velocity is measured at mid depth of current water body or 0.5m below water level.
- 3.33 Water depths are determined prior to measurement, using a portable battery operated depth detector, brand named 'Eagle Sonar', if the depths exceed 1.5 meter. If the depth between 1.5 meter and 1 meter, plastic tape measurement tied with appropriate weight are used the depth estimation. For the depths well below 1 meter, an appropriate steel ruler or rope with appropriate weight are used for the depth measurement.



DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.34 The impact monitoring data are handled by the ET's systematic data recording and management, which complies with in-house Quality Management System. Standard Field Data Sheets (FDS) are used in the impact monitoring program.
- 3.35 The monitoring data recorded in the equipment e.g. noise meter and Multi-parameter Water Quality Monitoring System are downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data are input into a computerized database properly maintained by the ET. The laboratory results are input directly into the computerized database and QA/QC checked by personnel other than those who input the data. For monitoring activities require laboratory analysis, the local laboratory follows the QA/QC requirements as set out under the HOKLAS scheme for all laboratory testing.

OTHERS MONITORING IMPLEMENTATION FOR THE CONTRACT

Ecology

3.36 Ecological monitoring and reporting should be performed by IEC. No equipment and procedure are presented in the EM&A Monthly Report.

Landscape and Visual

3.37 A registered Landscape Architect as member of the ET is employed by the Contractor to undertake site inspection. Site inspection will undertake at least once every two weeks throughout the construction period to ensure compliance with the intended aims of the mitigation measures are proposed in the EIA and the updated EM&A Manual, implemented by the Contractor.

DETERMINATION OF ACTION/LIMIT (A/L) LEVELS

3.38 The re-established performance criteria for construction noise, water quality and hydrological, namely Action and Limit levels is used for Contract 2 are listed in *Tables 3-5*, *3-6*, and *3-7*.

Table 3-5 Action and Limit Levels for Construction Noise

Location	Time Period	Action Level in dB(A)	Limit Level in dB(A)
	Daytime 0700 – 1900 hrs on normal weekdays	When one	75* dB(A)
M1, AL1, M2, M3, M4	1900 – 2300 on all days and 0700 – 2300 on general holidays (including Sundays	documented complaint is	60/65/70 dB(A)**
	2300 – 0700 on all days	received	45/50/55 dB(A)**

Note: * Reduces to 70dB(A) for schools and 65dB(A) during the school examination periods.

Table 3-6 Action and Limit Levels for Water Quality

Danamatan	Performance	I	mpact Station	n
Parameter	Criteria	W1	W2	W4
DO Concentration (mg/L)	Action Level	7.27	7.26	9.27
DO Concentration (mg/L)	Limit Level	4.00	4.00	4.00
all	Action Level	NA	NA	NA
pН	Limit Level	6 - 9	6 - 9	6 - 9
Tyshidity (NTII)	Action Level	4.77	2.46	3.32
Turbidity (NTU)	Limit Level	5.26	3.42	4.52
Suspended Solids (mg/L)	Action Level	9.73	8.89	6.98
Suspended Solids (mg/L)	Limit Level	10.77	9.75	7.66

^{**} To be selected based on the Area Sensitivity Rating of A/B/C, and the conditions of the applicable CNP(s) must be followed



Notes:

- The proposed Action/Limit Levels of DO are established to be used 5%-ile/1%-ile of all the baseline data:
- The proposed Action/Limit Levels of Turbidity and SS are established to be used 95%-ile/99%-ile of all the baseline data;
- For DO, non-compliance of the water quality limits occur is when monitoring result lower than the action/limit levels:
- For turbidity and SS, non-compliance of the water quality limits occurs is when monitoring result higher than the limits; and
- For pH, non-compliance of the quality limit occur is when monitoring result lower than 6 and higher than 9: and
- All the figures given in the table are used for reference only and the EPD may amend the figures whenever it is considered necessary

Table 3-7 Action and Limit Levels for Hydrological Characteristics

Parameter	Acceptance	Monitoring Station				
Parameter	Criteria	H1	H2			
Water Depth	Action Level	0.08 (80% of baseline water depth)	0.40 (80% of baseline water depth)			
(m)	Limit Level	0.06 (60% of baseline water depth)	0.30 (60% of baseline water depth)			
Volumetric	Action Level	120% of control station's water flow rate on the same day of measurement	120% of control station's water flow rate on the same day of measurement			
Flow Rate (Q), m ³ /s	Limit Level	140% of control station's water flow rate on the same day of measurement	140% of control station's water flow rate on the same day of measurement			

- 3.39 The locations H3 and H4 are a reference measurement point in order to monitor any changes in the hydrological characteristics of Wai Ha River arising from the work Contract 2 to affect the Shuen Wan Marsh.
- 3.40 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan enclosed in *Appendix F*.

EQUIPMENT CALIBRATION

- 3.41 The sound level meter and calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme in yearly basis.
- 3.42 All the water quality monitoring equipment such as the DO, pH and Turbidity meters are calibrated by HOKLAS accredited laboratory of three month intervals.
- 3.43 A portable, water flow meter, brand named "GLOBAL WATER model FP211" is calibrated in yearly basis.
- 3.44 All updated calibration certificates of the monitoring equipment used for the impact monitoring program in this Reporting Period are attached in *Appendix E*.

METEOROLOGICAL INFORMATION

3.45 The meteorological information during the construction phase is obtained from Tai Po and Shatin Stations of the Hong Kong Observatory (HKO). The meteorological data during the impact monitoring days are summarized in *Appendix H*



4.0 IMPACT MONITORING RESULTS

4.01 The monitoring schedule had been issued to relevant parties before each Reporting Period which presented in *Appendix G*. The works undertaken during the Reporting Period are illustrated in *Appendix C*. The monitoring results are presented in the following sub-sections.

MONITORING RESULTS SHARING

4.02 Environmental Permit EP-203/2008 was issued on 25 February 2008 by EPD which adopted for both Contracts 1 and 2 of DSD construction at Shuen Wan. Also, the EM&A programme of both contracts are undertaken in accordance with the same updated EM&A Manual which has to be carried out during construction period. According to the updated EM&A manual, designated monitoring Locations M1 and AL1 for noise monitoring stations, Locations W1 and W2 for water quality monitoring stations, and Locations H1 and H2 for hydrological measurement are requested to perform at both Contracts 1 and 2. Since Contract 1 has already commenced in January 2011, those results measured by Contract 1 would be shared for the Contract 2. This recommendation has been accepted by IEC and submitted to EPD.

RESULTS OF CONSTRUCTION NOISE MONITORING

4.03 In this Reporting Period, the noise monitoring results at the designated locations M1, AL1, M2, M3 and M4 are summarized in *Table 4-1*. The detail monitoring data are presented in *Appendix I*. The graphical plot is shown in *Appendix J*.

Table 4-1 Summary of Construction Noise Monitoring Results, dB(A)

Date	$L_{ m eq(30m)}$	in) (dB(A)	Date	$L_{eq(30min)}(dB(A)$			
Date	M1 ^(#)	AL1 ^(#)	Date	M2 ^(*)	M3 ^(*)	M4 ^(*)	
3-Apr-13	64.3	66.1	5-Apr-13	63.8	64.6	57.4	
10-Apr-13	63.6	63.5	8-Apr-13	71.4	67.5	57.9	
17-Apr-13	66.9	68.3	19-Apr-13	74.8	65.7	52.6	
24-Apr-13	61.8	62.1	24-Apr-13	67.5	65.1	62.8	
Limit Level	75 dB(A)						

Remarks:

- (#) The monitoring is undertaken under façade situation. No façade correction is added according to acoustical principles and EPD guidelines.
- The monitoring is undertaken under free field situation. A façade correction of +3 dB(A) has
- been added according to acoustical principles and EPD guidelines
- 4.04 The sound meter was set in a free field situation at the designated monitoring locations M2, M3 and M4, therefore, a façade correction of +3 dB(A) has been added according to acoustical principles and EPD guidelines. For Location A1 and AN1, the monitoring is undertaken under façade situation. No façade correction is added according to acoustical principles and EPD guidelines.
- 4.05 No noise complaint (which is an Action Level exceedance) was received in this Reporting Period. As shown in *Table 4-1*, all the noise monitoring result are well below 75dB(A) and no Action or Limit Level exceedance was triggered during this Reporting Period. The graphical plot is shown in *Appendix J*.

RESULTS OF LOCAL STREAM WATER QUALITY MONITORING

- 4.06 In this Reporting Period, **12** sampling days were performed at designated measurement Points W1 W2, W3 & W4 for local stream water quality monitoring. The monitoring results including in-situ measurements and laboratory testing results are provided in *Appendix I*. The graphical plots are shown in *Appendix J*.
- 4.07 Monitoring results of 3 key parameters: dissolved oxygen (DO), turbidity and suspended solids in this Reporting Period, are summarized in *Tables 4-2 and 4-3*.



Table 4-2 Water Quality Results Summary for W1 & W2

Compling]	DO (mg/L)		Turb	idity (NT	U)		SS (mg/L)	
Sampling date	W1 (ebb)	W1 (flood)	W2	W1 (ebb)	W1 (flood)	W2	W1 (ebb)	W1 (flood)	W2
3-Apr-13	7.08	6.93	7.18	6.4	5.9	2.1	9.00	10.00	1.20
5-Apr-13	6.77	7.56	7.88	4.4	<u>5.5</u>	2.8	<u>26.00</u>	33.00	2.00
8-Apr-13	6.84	6.12	7.89	10.0	7.0	3.2	34.00	10.00	1.00
10-Apr-13	5.35	5.24	7.48	19.1	20.7	<u>7.9</u>	11.00	11.00	<u>15.00</u>
12-Apr-13	5.80	5.92	8.06	4.3	4.6	3.3	5.00	5.00	4.80
15-Apr-13	5.58	5.40	7.13	1.9	1.8	2.5	6.00	7.00	8.40
17-Apr-13	5.41	4.90	6.86	<u>5.7</u>	6.0	<u>5.6</u>	<u>11.00</u>	12.00	3.40
19-Apr-13	6.11	5.64	6.89	20.3	20.0	2	<u>17.00</u>	16.00	2.60
22-Apr-13	4.85	4.63	6.79	6.2	5.8	2.9	8.00	9.00	6.20
24-Apr-13	8.27	6.81	7.34	7.0	1.5	6.9	25.00	2.00	13.00
26-Apr-13	4.79	5.67	7.78	10.9	8.9	2	<u>51.00</u>	9.00	4.80
29-Apr-13	6.14	5.21	7.71	4.3	0.9	3	13.00	24.00	5.60

[•] Bold and Italic is indicated exceeded Action Level; Bold with underline is indicated exceeded Limit Level

Table 4-3 Water Quality Results Summary for W3 & W4

Sampling	DO (DO (mg/L)		ty (NTU)	SS ((mg/L)
date	W3	W4	W3	W4	W3	W4
3-Apr-13	6.87	6.35	4.15	7.30	26.00	84.00
5-Apr-13	7.37	7.41	6.84	8.05	4.00	<u>15.00</u>
8-Apr-13	6.67	7.48	12.60	4.15	80.00	7.00
10-Apr-13	5.39	5.30	1.88	22.20	2.00	14.00
12-Apr-13	6.53	6.32	6.07	7.18	10.00	8.00
15-Apr-13	5.46	5.26	2.09	48.25	3.00	30.00
17-Apr-13	6.02	6.96	4.30	8.26	4.00	4.00
19-Apr-13	5.72	5.59	6.58	16.85	13.00	14.00
22-Apr-13	5.61	5.28	4.34	29.80	2.00	16.00
24-Apr-13	7.34	6.96	12.80	7.75	51.00	32.00
26-Apr-13	5.53	5.49	12.95	48.60	29.00	59.00
29-Apr-13	4.75	5.74	0.27	4.82	2.00	6.00

Bold and Italic is indicated exceeded Action Level; Bold with underline is indicated exceeded Limit Level

- 4.08 During the Reporting Period, field measurements showed that stream water temperatures were within 19.50°C to 26.50°C and pH values within 7.32 to 8.92.
- 4.09 A statistics of exceedances for the three parameters: dissolved oxygen (DO), turbidity and suspended solids are shown in *Table 4-4*.

 Table 4-4
 Statistics Water Quality Exceedance

Ctation	DO		Turbidity		SS		Total Exceedance	
Station	Action	Limit	Action	Limit	Action	Limit	Action	Limit
W1	22	0	0	16	2	13	24	29
W2	5	0	6	3	0	2	11	5
W4	12	0	1	11	1	9	14	20
No. of Exceedance	39	0	7	30	3	24	49	54

- 4.10 As shown in *Table 4-4*, a total of 103 Action/ Limit Level exceedances, namely 39 exceedances in dissolved oxygen, 37 exceedances in turbidity and 27 exceedances in suspended solids were recorded in this Reporting Period. NOEs were issued to notify EPD, IEC, the Contractor and RE upon confirmation of the results.
- 4.11 According to site information provided by the Contractor, the site activities undertaken on site included laying geotextile and rockfill; concreting blinding layer; fixing steel reinforcement;



erection of formwork; removal of sheetpile and backfilling.

- 4.12 In the Reporting Period, no excavation work was carried out at the channel, however, heavy rainstorm was occurred on 3, 5, 10, 12, 17, 19 and 26 April 2013 which increased the turbidity and suspended solids levels of the stream course by washed out from exposed slope and surface. To minimize the impact to the existing stream, precautionary measures such as earth bund to isolate the working area has been implemented on-site. The investigation results for the exceedances are summarized as follows:
 - For the DO exceedances, the construction activities comprised none of DO depleting characteristics. Therefore, it is considered that all the DO exceedances were due to natural variation of the stream and not related to the works under the Project.
 - During the water quality monitoring on 3, 5, 10, 12, 17, 19 and 26 April 2013, muddy water was observed at W4 which caused by soil runoff from the site during rainstorm. It is concluded that the exceedances at W4 were partially due to the project. The Contractor should enhance the water quality mitigation measures such as covering all exposed slopes with geotextile to prevent surface runoff during inclement weather.
 - For monitoring points W1, it is noted that the water quality at W1 was affected by marine water that comes from the Tolo Harbour during flood tide. Therefore, it is considered that the exceedances in W1 were not related to the works under the Project.
- 4.13 During wet season, KLKJV is reminded to fully implement the required water quality mitigation measures in accordance with the updated EM&A Manual stipulation during construction under the Project. In particular when excavation and the associated box culvert construction works are undertaken near Wai Ha River, all construction wastewater or runoff generated from work area should be treated and drained to the designated discharge point. Moreover, as an effective water quality mitigation measure, the rock bund in the de-silting channel should be repaired regularly and ensure the de-silting performance.

RESULTS OF HYDROLOGICAL CHARACTERISTICS MONITORING

4.14 In this Reporting Period, hydrological characteristics measurement at were carried out on 5, 12, 19 and 26 April 2013. The monitoring data of H1 and H2 provided by DC/2009/22 is showed *Appendix I*. The detailed H3 and H4 measurement results in this Reporting Period are presented in *Tables 4-5*.

Table 4-5 Detailed monitoring results of hydrological characteristics at H3 and H4

Date	Measurement Time	Tide Condition	River Width (m)	Water Depth (m)	Cut Section (m ²)	Velocity Flow Rate (m/s)	Average Volumetric Flow Rate (Q), m ³ /s		
Measurement Point: H3									
5 A 12	13:16	Flood	7.45	0.2	1.4900	0.1	0.149		
5-Apr-13	9:25	Ebb	7.45	0.2	1.4900	0.1	0.149		
10 4 12	9:00	Flood	7.45	0.3	2.2350	0.2	0.447		
12-Apr-13	13:30	Ebb	7.45	0.35	2.6075	0.2	0.522		
10 4 12	8:59	Flood	7.45	0.2	1.4900	0.2	0.298		
19-Apr-13	17:00	Ebb	7.45	0.25	1.8625	0.2	0.373		
26 Amm 12	17:09	Flood	7.45	0.2	1.4900	0.2	0.298		
26-Apr-13	12:30	Ebb	7.45	0.15	1.1175	0.2	0.224		
Measurem	ent Point: H4								
5 A 12	13:22	Flood	2.74	0.2	0.5480	0.2	0.110		
5-Apr-13	9:15	Ebb	2.74	0.15	0.4110	0.3	0.123		
10 4 12	9:06	Flood	2.74	0.2	0.5480	0.3	0.164		
12-Apr-13	13:20	Ebb	2.74	0.2	0.5480	0.3	0.164		
19-Apr-13	9:05	Flood	2.74	0.1	0.2740	0.1	0.027		



Date	Measurement Time	Tide Condition	River Width (m)	Water Depth (m)	Cut Section (m ²)	Velocity Flow Rate (m/s)	Average Volumetric Flow Rate (Q), m ³ /s
	17:15	Ebb	2.74	0.15	0.4110	0.2	0.082
26 Am 12	17:06	Flood	2.74	0.1	0.2740	0.3	0.082
26-Apr-13	12:15	Ebb	2.74	0.1	0.2740	0.3	0.082

4.15 Hydrological characteristics results of the all measurement points are summarized in *Tables 4-6* and *4-7*.

Table 4-6 Summarized Hydrological Characteristics of Water Depth, m

Doto		Mid-	Flood		Mid-Ebb			
Date	H1	H2	Н3	H4	H1	H2	Н3	H4
5-Apr-13	0.48	0.24	0.20	0.20	0.18	0.12	0.20	0.30
12-Apr-13	#	#	0.30	0.30	0.12	0.24	0.35	0.30
19-Apr-13	#	#	0.20	0.10	0.24	0.18	0.25	0.20
26-Apr-13	#	#	0.20	0.30	0.24	0.18	0.15	0.30

[#] No data was provided by Contract 1.

Table 4-7 Summarized Hydrological Characteristics of Average Volumetric flow rate (Q), m³/s

Date		Mid-	Flood		Mid-Ebb			
	H1	H2	Н3	H4	H1	H2	Н3	H4
5-Apr-13	0.075	0.754	0.15	0.11	0.225	1.507	0.15	0.12
12-Apr-13	#	#	0.45	0.16	0.075	0.754	0.52	0.16
19-Apr-13	#	#	0.30	0.03	0.15	1.13	0.37	0.08
26-Apr-13	#	#	0.30	0.08	0.15	1.507	0.22	0.08

[#] No data was provided by Contract 1.

4.16 To compare the monitoring data between the Reporting Period (rainy season) and baseline monitoring period, the currently water depth and volumetric flow rate has insignificant changed. Furthermore, water depth and water flow rate were found no exceedance in this Reporting Period.

RESULTS OF ECOLOGICAL MONITORING

- 4.17 According to updated EM&A Manual Section 6.17, bi-monthly ecological monitoring is conducted by the IEC ENVIRON Hong Kong Limited. In brief, the monitoring tasks include regular check on the retained and transplanted trees and shrubs, monitoring on fauna groups and aquatic fauna within the works area and any ecologically sensitive area within 100 m of the works boundary.
- 4.18 In this Reporting Period, no the ecological monitoring in Area under Contract 2 is performed.



5.0 WASTE MANAGEMENT

5.01 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

RECORDS OF WASTE QUANTITIES

- 5.02 All types of waste arising from the construction work are classified into the following:
 - Construction & Demolition (C&D) Material;
 - Chemical Waste;
 - General Refuse; and
 - Excavated Soil.
- 5.03 The quantities of waste for disposal in this Reporting Period are summarized in *Table 5-1* and *5-2* and the Monthly Summary Waste Flow Table is shown in *Appendix K*. Whenever possible, materials were reused on-site as far as practicable.

Table 5-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity	Disposal Location
C&D Materials (Inert) (m ³)	0	-
Reused in this Contract (Inert) (m ³)	0	-
Reused in other Projects (Inert) (m ³)	0	-
Disposal as Public Fill (Inert) (m ³)	310	Tuen Mun Area 38

Table 5-2 Summary of Quantities of C&D Wastes

Type of Waste	Quantity	Disposal Location
Recycled Metal (kg)	0	-
Recycled Paper / Cardboard Packing (kg)	0	-
Recycled Plastic (kg)	0	-
Chemical Wastes (kg)	0	-
General Refuses (m ³)	5	Local refuse station

5.04 To control over the site performance on waste management, the Contractor shall ensure that all solid and liquid waste management works are in full compliance with the relevant license/permit requirements, such as the effluent discharge license and the chemical waste producer registration. The Contractor is also reminded to implement the recommended environmental mitigation measures according to the EM&A Manual based on actual site conditions.



6.0 SITE INSPECTION

REGULAR SITE INSPECTION AND MONTHLY AUDIT

- According to the Updated Environmental Monitoring and Audit Manual, regular site inspection to evaluate the project environmental performance should be carried out during construction phase. Weekly environmental site inspections had been carried out by the Contractor, ET and RE on 3, 10, 17 and 26 April 2013. Also, joint site inspection with the IEC was carried out on 26 April 2013. In this Reporting period, 4 observations were recorded but no non-compliance was noted.
- 6.02 Observations for the site inspection and monthly audit within this Reporting Period are summarized in *Table 6-1*.

Table 6-1 Site Inspection of Observations – Findings and Deficiencies

Date	Findings / Deficiencies	Follow-Up Status
3 April 2013	• As a reminder, stagnant water cumulated on site during the rainstorm, the contractor was reminded to remove the stagnant water cumulated on site after the rainstorm.	Not required for reminder.
10 April 2013	• Turbid water from the upstream was observed during the rainstorm. The Contractor should check the water mitigation measures at the upstream works area more frequency after the rainstorm to maintain the efficiency.	Rectified on 17 April 2013.
17 April 2013	• No adverse environmental issue was observed during site inspection.	N.A.
26 April 2013	 Chemical containers without drip tray were observed at the upstream area, the contractor was reminded to provide drip tray for all chemical containers in the site area to prevent leakage. De-silting tank at the upstream area was observed full of sediment, the contractor was reminded to clean more frequency to maintain the efficiency. Soil and mud was observed at the public road near the works area, the contractor was reminded to clean and maintain the public area near the site clean and tidy. 	To be followed in May 2013.

LANDSCAPE AND VISUAL INSPECTION

- 6.03 In this Reporting Period, landscape and visual inspection was carried on 5, 18 and 30 April 2013.
- 6.04 The stand-alone of monthly Landscape & Visual Report signed by the registered Landscape Architect. Mitigation measures implemented in this Reporting Period are presented in the monthly Landscape & Visual Report (April 2012) which enclosed in Appendix L.
- 6.05 The next bi-weekly Landscape & Visual Monitoring in May 2013 is scheduled to be conducted in the week of 13 and 29 May 2013.



7.0 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

7.01 No environmental complaint, summons and prosecution was received in this Reporting Period. The statistical summary table of environmental complaint is presented in *Tables 7-1*, 7-2 and 7-3.

Table 7-1 Statistical Summary of Environmental Complaints

Donauting Davied	Envi	ronmental Complaint S	tatistics
Reporting Period	Frequency	Cumulative	Complaint Nature
July 2011 – March 2013	0	0	NA
April 2013	0	0	NA

Table 7-2 Statistical Summary of Environmental Summons

Donorting Donied	Envi	ronmental Summons S	tatistics
Reporting Period	Frequency	Cumulative	Complaint Nature
July 2011 – March 2013	0	0	NA
April 2013	0	0	NA

Table 7-3 Statistical Summary of Environmental Prosecution

Donauting Daviad	Enviro	onmental Prosecution S	Statistics
Reporting Period	Frequency	Cumulative	Complaint Nature
July 2011 – March 2013	0	0	NA
April 2013	0	0	NA



8.0 IMPLEMENTATION STATUS OF MITIGATION MEASURES

8.01 The environmental mitigation measures that recommended in the Updated Environmental Monitoring and Audit Manual covered the issues of dust, noise and waste and they are summarized as follows:

Noise Mitigation Measure

- (a) Only well-maintained plant should be operated on-site and plant shall be serviced regularly during the construction program;
- (b) Silencers or mufflers on construction equipment should be utilized and shall be properly maintained during the construction program;
- (c) Mobile plant, if any, should be sited as far from NSRs as possible;
- (d) Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;
- (e) Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs;
- (f) Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities;
- (g) Use of quieter plants to carry out the construction tasks proposed for the Project;
- (h) Use about 3.5m high of temporary noise barriers as screened the noisy PMEs to carry out construction of box culvert and site clearance.
- (i) Low Impact Method, such as using PMEs smaller in size and to be enclosed by noise enclosure, should be adopted for the construction of box culvert and pipe laying in Wai Ha; and
- (j) Use of noise enclosure during the works area for pipe laying in Wai Ha.

Dust Mitigation Measure

- 8.02 Implementation of mitigation measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices including but not limited to the following:
 - (a) Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved road, with complete coverage, particularly during dry weather;
 - (b) Use of frequent watering for particularly dusty static construction areas and areas close to ASRs;
 - (c) Tarpaulin covering of all dusty vehicle loads transported to, from and between site location;
 - (d) Establishment and use of vehicle wheel and body washing facilities at the exit points of the site;
 - (e) Routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs:
 - (f) Stockpiled excavated materials should be covered with tarpaulin and should be removed offsite within 24 hours to avoid any odour nuisance arising.

Local Stream Water Quality Mitigation Measure

- (a) Before commencing any site formation work, all sewer and drainage connections shall be sealed to prevent debris, soil, sand etc. from entering public sewers/drains;
- (b) Temporary ditches shall be provided to facilitate run-off discharge into appropriate watercourses, via a silt retention pond. No site run-off shall enter the fishponds at Shuen Wan;
- (c) Sand/silt removal facilities such as sand traps, silt traps and sediment basins shall be provided to remove sand/silt particles from runoff to meet the requirements of the Technical Memorandum standard under the Water Pollution Control Ordinance. The design of silt removal facilities shall be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures shall be inspected monthly and maintained to ensure proper and efficient operation al all times and particularly during rainstorms
- (d) Water pumped out from excavated pits shall be discharged into sill removal facilities;

DSD Contract No. Contract No. DC/2010/02 - Drainage Improvement in Shuen Wan and Shek Wu Wai





- (e) During rainstorms, exposed slope/soil surfaces shall be covered by a tarpaulin or other means. Other measures that need to be implemented before, during, and after rainstorms as summarized in ProPECC PN 1/94 shall be followed
- (f) Exposed soil areas shall be minimized to reduce potential for increased siltation and contamination of runoff
- (g) Earthwork final surfaces shall be well compacted and subsequent permanent work or surface protection shall be immediately performed to reduce the potential of soil erosion;
- (h) Open stockpiles of construction materials or construction wastes on-site shall be covered with tarpaulin or similar fabric during rainstorms;
- (i) For the construction of the box culvert next to the existing channel of the Wai Ha River, sand bags should be deployed around the boundary of the works trench to prevent muddy water ingress into the adjacent CA or Wai Ha River. Sand bags should also be used to surround the excavated trench. Generally, the sand bags will be placed up to a height 01 300mm to provide adequate allowance for the built-up water level during rainstorm event. With sand bags in place surface runoff will be intercepted and flow to Wai Ha River or collected by the existing drainage system as usual;
- (j) For the construction of the box culvert in the extreme northeast corner of Shuen Wan Marsh Conservation Area sand bags should be deployed along the limit of the works area to prevent muddy water ingress into the CA. Sand bags should be placed to a height 0.1 at least 300mm from ground level and +2.5 mPD (whichever is greater) to provide adequate allowance for the built-up water level during rainstorm events Unpolluted surface runoff within the works area should then be collected and directed into the existing drainage system;
- (k) Sheet-piles, which would be installed around the works trench near the Conservation Area, would be extended above ground level for about 2m to serve as hoardings to isolate the works site;
- (l) Tarpaulin sheets would be used to cover the excavation areas during heavy rainstorms. This would prevent the ingress of rainwater into the trench minimizing the risk of muddy water getting into Wai Ha River and the adjacent Conservation Area;
- (m) Any concrete washing water would be contained inside the works site surrounded by the extended sheet piles. A pump sump at the bottom 0f the trench would be provided to pump any excess water during concrete washing;
- (n) Stockpiling the excavated materials adjacent to the Conservation Area would not be allowed. The excavated materials would be either removed off site immediately after excavation, or stockpile at location(s) away from the Conservation Area. The stockpile locations shall be approved by the site engineer;
- (o) Debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering the Wai Ha River and fish ponds at Shuen Wan. Stockpiles of cement and other construction materials should be kept covered when not being used.
- (p) Oils and fuels should only be used and stored in designated areas which have pollution prevention facilities to prevent spillage of fuels and solvents to nearby water bodies, all fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity 01 the largest tank The bund should be drained of rainwater after a rain event
- (q) Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities:
- (r) The excavation works within the upstream end of the existing river channel of the Wai Ha River for the construction of the proposed box culvert should be carried out in dry condition. Containment measures such as bunds and barriers shall be used within the affected length of the river channel and the excavation works restricted to within an enclosed dry section of the channel. The excavation works within Wai Ha River shall be restricted to the period from October to April.



Waste Mitigation Measures

- (a) The Contractor shall observe and comply with the Waste Disposal Ordinance (WDO) and its subsidiary regulations.
- (b) The Contractor shall submit to the Engineer for approval a Waste Management Plan with appropriate mitigation measures including the allocation of an area for waste segregation and shall ensure that the day-to-day site operations comply with the approved waste management plan.
- (c) The Contractor shall minimize the generation of waste from his work. Avoidance and minimization of waste generation can be achieved through changing or improving design and practices, careful planning and good site management.
- (d) The reuse and recycling of waste shall be practised as far as possible. The recycling materials shall include paper/cardboard, timber and metal etc.
- (e) The Contractor shall ensure that Construction and Demolition (C&D) materials are sorted into public fill (inert portion) and C&D waste (non-inert portion). The public fill which comprises soil, rock, concrete, brick, cement plaster/mortar, inert building debris, aggregates and asphalt shall be reused in earth filling, reclamation or site formation works. The C&D waste which comprises metal, timber, paper, glass, junk and general garbage shall be reused or recycled where possible and, as the last resort, disposal of at landfills.
- (f) The Contractor shall record the amount of wastes generated, recycled and disposed of (including the disposal sites). The Contractor shall use a trip ticket system for the disposal of C&D materials to any designated public filling facility and/or landfill.
- (g) In order to avoid dust or odour impacts, any vehicles leaving a works area carrying construction waste or public fill shall have their load covered.
- (h) To avoid the excessive use of wood, reusable steel shutters shall be used as a preferred alternative to formwork and falsework where possible.
- (i) The Contractor shall observe and comply with the Waste Disposal (Chemical Waste) (General) Regulation. The Contractor shall apply for registration as chemical waste producer under the Waste Disposal (Chemical Waste) (General) Regulation when chemical waste is produced. All chemical waste shall be properly stored, labeled, packaged and collected in accordance with the Regulation.
- 8.03 KLKJV had been implementing the required environmental mitigation measures according to the Updated Environmental Monitoring and Audit Manual subject to the site condition. Environmental mitigation measures generally implemented by KLKJV in this Reporting Period are summarized in *Table 8-1*.

Table 8-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Water Quality	 Wastewater were appropriately treated by treatment facilities; Drainage channels were provided to convey run-off into the treatment facilities;
	 and Drainage systems were regularly and adequately maintained.
Air Quality	 Regular watering to reduce dust emissions from all exposed site surface, particularly during dry weather; Frequent watering for particularly dusty construction areas and areas close to
	 air sensitive receivers; Cover all excavated or stockpile of dusty material by impervious sheeting or
	 cover an excavated of stockpile of dusty inaterial by impervious sheeting of sprayed with water to maintain the entire surface wet; Public roads around the site entrance/exit had been kept clean and free from
	dust; and
	Tarpaulin covering of any dusty materials on a vehicle leaving the site.
Noise	 Good site practices to limit noise emissions at the sources; Use of quite plant and working methods;
	Use of site hoarding or other mass materials as noise barrier to screen noise at ground level of NSRs;
	• Use of shrouds/temporary noise barriers to screen noise from relatively static PMEs;
	 Scheduling of construction works nearly Tung Tsz Road; and
	Alternative use of plant items within one worksite, where practicable.

DSD Contract No. Contract No. DC/2010/02 - Drainage Improvement in Shuen Wan and Shek Wu Wai





Issues	Environmental Mitigation Measures
Chemical Management	 Excavated material should be reused on site as far as possible to minimize off-site disposal. Scrap metals or abandoned equipment should be recycled if possible; Waste arising should be kept to a minimum and be handled, transported and disposed of in a suitable manner; The Contractor should adopt a trip ticket system for the disposal of C&D materials to any designed public filling facility and/or landfill; and Chemical waste shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes.
General	The site was generally kept tidy and clean.

22nd Monthly EM&A Report –April 2013



9.0 IMPACT FORCAST

CONSTRUCTION ACTIVITIES FOR THE FORTH-COMING MONTH

- 9.01 Construction activities planned to be carried out next month at Shuen Wan is listed as below:-
 - Construction of Box Culvert Bay 44-50 & intake structure
 - Construction of Wai Ha Box Culvert Bay 2, 9, & 10
- 9.02 Three months Rolling Construction Program is attached in *Appendix C*

KEY ISSUES FOR THE COMING MONTH

- 9.03 According to construction activities carry out in coming months, key issues to be considered include:
 - Implementation of dust suppression measures at all times;
 - Ensure dust suppression measures are implemented properly;
 - Disposal of empty engine oil containers within site area;
 - Sediment catch-pits and silt removal facilities should be regularly maintained;
 - Management of chemical wastes;
 - Discharge of site effluent to the nearby local stream or storm drainage, stockpiling or disposal of materials, and any dredging or construction area at this area are prohibited;
 - Follow-up of improvement on general waste management issues; and
 - Implementation of construction noise preventative control measures.

22nd Monthly EM&A Report –April 2013



10.0 CONCLUSIONS AND RECOMMENTATIONS

CONCLUSIONS

- 10.01 This is the 22nd monthly EM&A report for Contract 2 presenting the monitoring results and inspection findings for the Reporting Period from 1 to 30 April 2013.
- 10.02 No noise complaint (which is an Action Level exceedance) was received and no construction noise measurement results that exceeded the Limit Level were recorded in this Reporting Period. No NOE or the associated corrective actions were therefore issued.
- 10.03 For water quality monitoring, a total of 103 Action/ Limit Level exceedances, namely 39 exceedances in dissolved oxygen, 37 exceedances in turbidity and 27 exceedances in suspended solids were recorded in this Reporting Period. It is concluded that the exceedances at W4 were partially due to the project. The Contractor should enhance the water quality mitigation measures such as covering all exposed slopes to prevent surface runoff in case of inclement weather.
- 10.04 The hydrological characteristics of water depth and water flow rate were found no exceedance in this Reporting Period.
- 10.05 In this Reporting Period, no ecological monitoring in Area under Contract 2 was performed.
- 10.06 No documented complaint, notification of summons or successful prosecution was received.
- 10.07 Weekly environmental site inspections had been carried out by the Contractor, ET and the RE on 3, 10, 17 and 26 April 2013. Furthermore, joint site inspection with the IEC was carried out on 26 April 2013. In this Reporting Period, 4 observations were recorded but no non-compliance was noted during the site inspection.
- 10.08 In this Reporting Period, landscape and visual inspection was carried on 5, 18 and 30 April 2013 and the monthly Landscape & Visual Report (April 2013) has been signed by the registered Landscape Architect.


RECOMMENDATIONS

- 10.09 As excavation works of construction box culvert or a trench, surface runoff or water discharge to local stream course should be key environment aspect issue. The Contractor is reminded that mitigation measures for water quality and ecology should be fully implemented. As an effective water quality mitigation measure, the rock bund in the de-silting channel should be repaired regularly and ensure the de-silting performance.
- 10.10 During wet season, muddy water and other water quality pollutants via site surface water runoff into the local stream Wah Ha River would be the key issue in the forth-coming month. On the other hand, construction noise should be other key environmental issue during sheet-piling process. The noise mitigation measures should be necessary to implement in accordance with EM&A Manual stipulation. Dust mitigation measures to avoid fugitive dust emissions from loose soil surface or haul road is also reminded.
- 10.11 To control the site performance on waste management, the KLKJV shall ensure that all solid and liquid waste management works are fully in compliance with the relevant license/permit requirements, such as the effluent discharge licence and the chemical waste producer registration. KLKJV is also reminded to implement the recommended environmental mitigation measures according to the Updated Environmental Monitoring and Audit Manual.



Appendix A

Site Location Plan (DSD Contract 1 and Contract 2 at Shuen Wan)

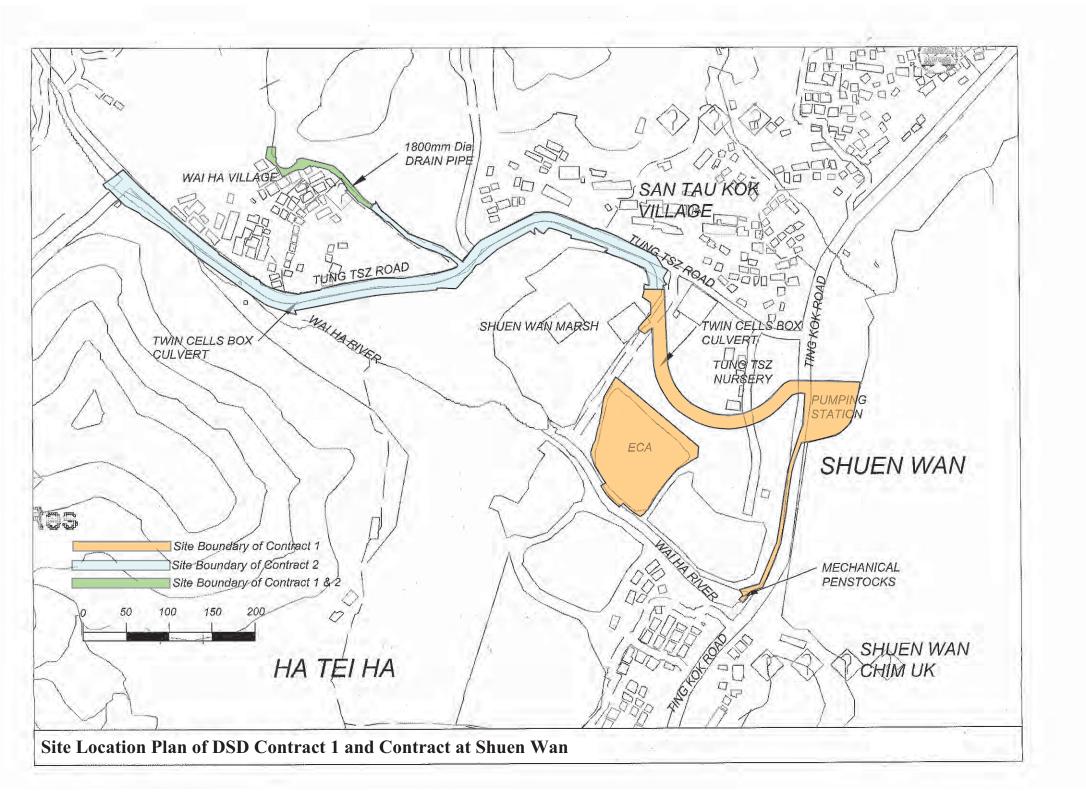




Appendix B

Organization Chart and the Key Contact Person



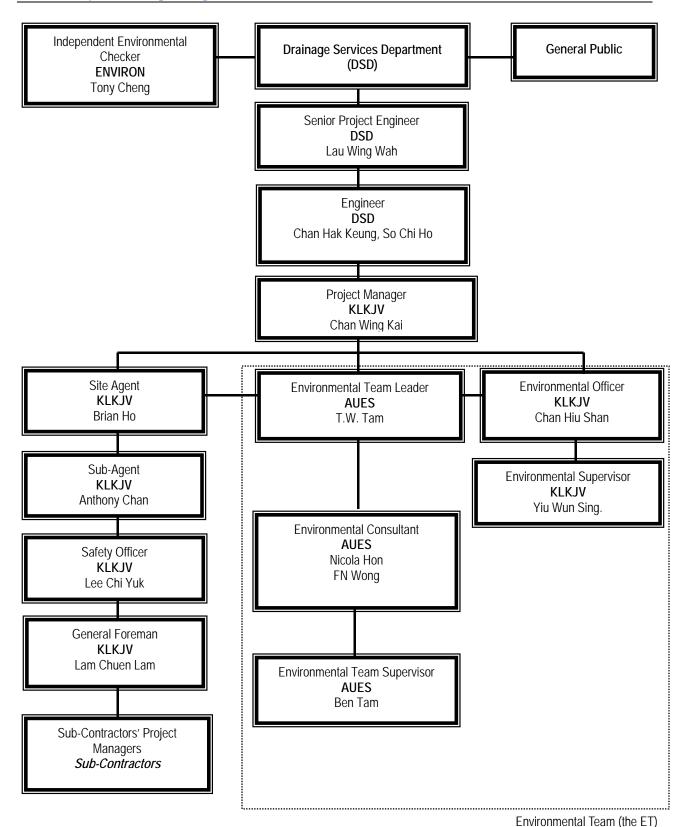

Environmental Management Organization



Contact Details of Key Personnel

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
DSD	Employer	Mr. Luk Wai Hung	2594 7400	2827 8700
DSD	Senior Engineer	Mr. Lau Wing Wah	2594 7402	2827 8700
DSD	Engineer	Mr. Chan Hak Keung	2594 7596	2827 8700
DSD	Engineer	Mr. So Chi Ho	2594 7356	2827 8700
DSD	Senior Inspector	Mr. Tso Si On	6778 2708	2827 8700
ENVIRON	Independent Environmental Checker	Mr. Tong Cheng	3465-2888	3465-2899
KLKJV	Project Director	Mr. Poon Chi Yeung Francis	2674 3888	2674 9988
KLKJV	Project Manager	Mr. Chan Wing Kai	2674 3888	2674 9988
KLKJV	Site Agent	Mr. Brian Ho	2674 3888	2674 9988
KLKJV	Sub- Agent	Mr. Anthony Chan	2674 3888	2674 9988
KLKJV	Technical Manager	Mr. Yeung Tai Yung	9674 9712	2674 9988
KLKJV	Site Forman	Mr. Lam Chuen Lam	2674 3888	2674 9988
KLKJV	Environmental Officer	Miss. Chan Hiu Shan	2674 3888	2674 9988
KLKJV	Environmental Supervisor	Mr. Yiu Wun Sing	2674 3888	2674 9988
AUES	Environmental Team Leader	Mr. T.W. Tam	2959-6059	2959-6079
AUES	Senior Environmental Consultant	Mr. Wong Fu Nam	2959-6059	2959-6079
AUES	Environmental Consultant	Miss. Nicola Hon	2959-6059	2959-6079
AUES	Environmental Supervisor	Mr. Ben Tam	2959-6059	2959-6079

Legends:

DSD (Employer) – Drainage Services Department

DSD (Engineer) – Drainage Services Department

KLKJV (Main Contractor) – Kwan Lee-Kuly Joint Venture


ENVIRON (IEC) – ENVIRON Hong Kong Limited

AUES (ET) – Action-United Environmental Services & Consulting





Appendix C


Master Construction Programs

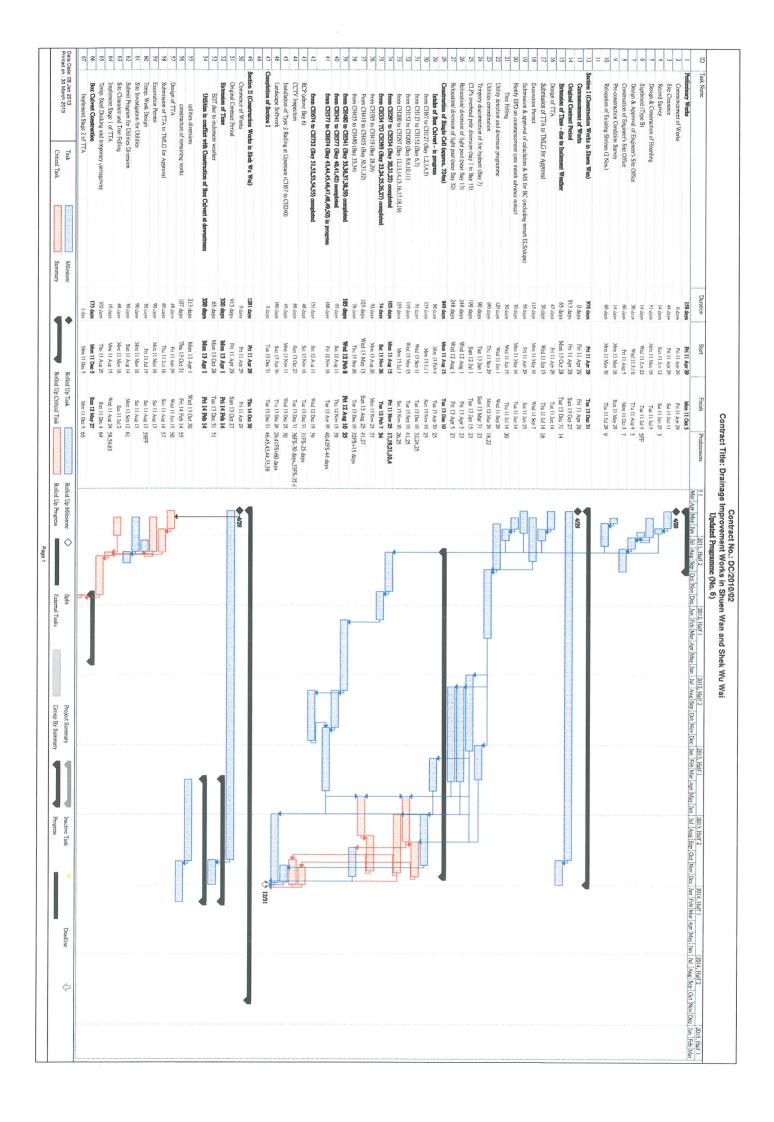


Search (1979) Search (1979) Search (1979) Search (1970) Se	Wed 13 May 22 Mon 13 Aer 1 Mon 12 May 14 Wed 13 May 1 Mon 12 May 14 Mon 13 May 12 Mon 13 Mon 23 Mon 13 Mon 24 Mon 13 Mon 26 Mon 13 Mon	90 days 11 days 12 days 12 days 13 days 14 days 15 days 16 days 16 days 16 days 17 days 18 days 18 days 19 days 10 days 10 days 10 days 10 days 10 days 10 days 11 days 11 days 12 days 13 days 14 days 15 days 16 days 16 days 17 days 18 days 18 days 19 days 19 days 10 days	HGC - matholes & ducting construction works (near RW2) HGC - matholes & ducting construction works (near RW2) HGC - duction & charging over PCCW - HGC - duction & charging over PCCW - matholes & ducting construction works (near RW2) PCCW - matholes & ducting construction works (near RW2) PCCW - matholes & ducting construction works (near RW2) PCCW - diversion & charging over (cocact aboles) PCCW - diversion of comestion points PWSD - pipes frainfection, installation & laying (near RW2) PWSD - pipes frainfection, installation & laying (near RW2) PWSD - pipes frainfection, installation & laying (near RW2) PWSD - pipes frainfection, installation & laying (near RW2) PWSD - pipes frainfection, installation & laying (near RW2) PWSD - pipes frainfection, installation & laying (near RW2) PWSD - pipes frainfection, installation & laying (near RW2) PWSD - pipes frainfection, installation with PWSD PWSD - pipes frainfection, installation with PWSD PWSD - pipes frainfection, installation with PWSD PWSD - pipes frainfection, installation points PWSD - pipes frainfection of comection points PWSD - pipes frainfection of comection points PWSD - pipes frainfection points with PWSD PWSD - pip
92.00 90.97 91.01 92.106 95.107 95.108 96.99 96.99 97.00 97.	Wed 13 May 12 Men 13 May 14 Wed 13 May 14 Men 12 May 14 Men 12 May 14 Men 12 May 14 Men 12 May 16 Men 12 May 17 Men 12 May 18 Wed 13 May 1 Wed 13 May 1 The 12 Mey 22 Sai 12 New 2 Sai 12 Dec 15 The 12 New 2 Wed 12 Dec 2 Sai 12 Dec 2 Wed 12 Dec 2 Wed 12 Dec 2 Wed 12 Dec 2 Wed 13 May 2 The 13 May 2 The 13 May 2 The 13 May 2 The 13 May 3	90 days 60 days 70 days 71 days	HGC - manholes & ducting construction works (near RW2) HGC - manholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - APPlication PCCW - APPlication PCCW - manholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - diversion & changing over (local cables) PCCW - diversion of connection points PCCW - diversion of connection points PCCW - diversion of connection points with WSD PCCW - diversion of diseased piped reinhaltment PCD - swahling flushing sterilization WSD - diversion of 3 now din 27 pipes WSD - diversion of 3 now din 27 pipes PCCM- diversion of 4 pipes of the proper works PCCM- diversion of 5 now din 27 pipes PCCM-
92 90,007 91,101 97,100 98,100 98 98 98 80,100 100,100 101 101 101 101 101	Wed 13 May 12 Men 13 Aer 1 Wed 13 Jan 12 Wed 13 Jan 12 Wed 13 May 14 Men 12 May 14 Men 12 May 16 Men 12 May 17 Men 13 May 18 Wed 13 May 1 Wed 13 May 1 The 12 May 22 Sat 12 New 22 Sat 12 New 25 Sat 12 New 25 Sat 12 Dec 15 The 12 New 22 Wed 12 New 22 Wed 12 Dec 26 Wed 13 May 2 Thu 13 May 3 Thu 13 May 2 Thu 13 May 3	Oldoss Oldoss	HGC - manholes & ducting construction works (near RW2) HGC - manholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - PROCW - APPlication PCCW - Application PCCW - Application PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - diversion & changing over (local cables) PCCW - diversion of connection points with WSD WSD - pipes frainfaction, installation & laying (near RW2) WSD - pipes frainfaction, installation & laying (near RW2) WSD - pipes frainfaction, installation & laying (near RW2) WSD - pipes frainfaction, installation & laying (near RW2) WSD - pipes frainfaction, installation & laying (near RW2) WSD - pipes frainfaction, installation & laying (near RW2) WSD - pipes frainfaction, installation & laying (near RW2) WSD - pipes frainfaction, installation & laying (near RW2) WSD - pipes frainfaction, installation & laying (near RW2) WSD - pipes frainfaction, installation & laying (near RW2) WSD - pipes frainfaction points with WSD WSD - wabling flashing starting of connection of dissect pipes (refreshed with WSD WSD - wabling flashing starting of connection of connection points with WSD WSD - wabling flashing starting of connection of the pipes of connection
92 90,007 91,101 97,100 97,100 97,100 98,100 98,100 100,107 100,107 100,107 101 101 101 102,107 103 104 105 106 107 107 108 108 109 109 109 109 109 109 109 109	Wed 13 May 22 Mnn 13 Aer 1 Wed 13 Jan 12 Wed 13 Jan 12 Wed 13 May 1 Wed 13 Jan 18 Fei 13 Jan 18 Fei 13 Jan 18 Fei 13 Jan 18 Fei 13 Jan 18 Tei 12 New 22 Sat 12 New 25 Sat 12 Dec 15 Sat 12 Dec 15 Sat 12 Dec 26 Wed 13 Jan 29 Thu 13 Jan 20 Thu 13 Ja	olidos ol	HGC - manholes & ducting construction works (near RW2) HGC - manholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - PROCW - Adversion & changing over PCCW - Adversion & changing construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - diversion & changing pover (local cabbes) PCCW - diversion & changing over (local cabbes) PCCW - diversion of connection points with WSD WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation with WSD WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication points with WSD WSD - pipes frabrication points with WSD WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication points with WSD W
92.00 93.00 97.10	Wed 13 May 12 Mon 13 Aer 1 Wed 13 May 14 Mon 12 May 14 Mon 12 May 14 Mon 13 May 1 Mon 13 May 14 Mon 13 May 17 Mon 13 May 17 Mon 13 May 17 Mon 13 May 18 Wed 13 May 1 Wed 13 May 2 The 12 Mor 22 Sai 12 Nov 3 The 12 Nov 2 Sai 12 Nov 3 Sai 12 Doe 1 Sai 12 Doe 1 Sai 12 Doe 5 Wed 12 Doe 25 Wed 13 May 24 The 13 May 24 Th	90 days 653 days 653 days 653 days 654 days 654 days 654 days 655	HGC - matholes & ducting construction works (near RW1) HGC - matholes & ducting construction works (near RW2) HGC - diversion & charging over PCCW - Macholes & ducting construction works (near RW2) PCCW - matholes & ducting construction works (near RW2) PCCW - matholes & ducting construction works (near RW2) PCCW - diversion & charging over (local dables) PCCW - diversion of the formation of the syming (near RW2) WSD - material delivery WSD - exposition of connection points with WSD WSD - pipes frainfeaton, installation & laying (near RW2) WSD
92.00 93.10	Wed 13 May 22 Mnn 13 Arr 1 Mnn 12 May 14 Mnn 12 May 14 Mnn 12 May 14 Mnn 13 May 15 Fri 13 May 15 Fri 13 May 12 Mnn 13 May 22 Mnn 12 May 22 Mnn 12 May 22 Mnn 12 May 22 Mnn 12 May 22 Mnn 13 May 14 Mnn 13 May 15 Mnn 12 May 22 Mnn 12 Mnn 23 Mnn 12 Mnn 24 Mnn	90 days 60 days 60 days 60 days 60 days 60 days 70 days 71 day	HGC - matholes & ducting construction works (near RW1) HGC - matholes & ducting construction works (near RW2) HGC - diversion & charing enver PCCW - matholes & ducting construction works (near RW2) PCCW - maholes & ducting construction works (near RW2) PCCW - maholes & ducting construction works (near RW2) PCCW - diversion & charinging over (coact ables) PCCW - diversion of coaction of remaining Box Culvert WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication of non-ction points with WSD WSD - suspection of connection points with WSD WSD - suspection of susk accurate point and point with WSD WSD - suspection of susk accurate point with WSD WSD - suspection of connection points with WSD WSD - suspection of susk accurate point with WSD WSD - suspection of connection points with WSD WSD - suspection of susk accurate point with wspection points with wspect
92 90,007 92,100 95,102 95,102 95,102 95,102 95,102 95,102 102,105 103,107 104 105 106 106 107 108 108 108 108 108 108 108 108 108 108	Wed 13 May 12 Mm 13 Aer 1 Wed 13 Jan 12 Mm 12 May 14 Mm 12 May 14 Mm 12 May 14 Wed 13 May 1 Wed 13 May 1 Wed 13 May 1 Mm 12 May 14 Mm 12 May 14 Mm 12 May 14 Mm 13 May 16 Mm 12 May 16 Mm 13 May 17 Mm 12 May 18 Fri 13 Jan 19 Mm 12 May 22 Mm 12 May 23 Mm 12 May 24 Mm 12 May 25 Mm 12 May 26 Mm 12 Dac 26 Wed	90 days 60 days 60 days 60 days 60 days 60 days 90 days 90 days 90 days 11 days 12 days 12 days 13 days 14 days 15 days 16 days 16 days 17 days 16 days 16 days 16 days 17 days 18 days 18 days 19 days 19 days 19 days 19 days 10 day	HGC - matholes & ducting construction works (near RW2) HGC - matholes & ducting construction works (near RW2) HGC - diversion & charging over PCCW - Matholes & ducting construction works (near RW2) HGC - diversion & charging over (cold subtes) PCCW - matholes & ducting construction works (near RW2) PCCW - matholes & ducting construction works (near RW2) PCCW - matholes & ducting construction works (near RW2) PCCW - matholes & ducting pover (cold subtes) PCCW - diversion & charging pover (cold subtes) PCCW - diversion of connection points with WSD - pripes frabrication, installation & laying (near RW2) WSD - pripes frabrication, installation & laying (near RW2) WSD - pripes frabrication points with WSD wSD - pripes fr
92 90,007 91,101 92,102 95,102 95,102 96,102 96,102 97,103	Wed 13 May 22 Mnn 13 Aer 1 Wed 13 Jan 12 Mnn 12 May 14 Mrn 12 May 14 Mrn 12 May 14 Wed 13 May 1 Wed 13 May 1 Mnn 12 May 14 Mnn 12 May 14 Mnn 12 May 14 Mnn 12 May 14 Mnn 12 May 16 Mnn 12 May 18 Fri 13 Jan 18 Fri 13 Jan 18 Fri 13 Jan 18 Fri 13 Jan 18 Tru 12 May 22 Tru 12 May 22 Tru 12 New 23 Tru 12 New 25 Tru 12 New 25 Tru 12 New 25 Tru 12 New 27 Tru 12 New 27 Tru 12 New 27 Tru 12 New 28 Satt 12 Dec 1 Wed 13 Dec 20 Wed 12 Dec 20 Wed 12 Dec 20 Wed 12 Dec 20	90 days 683 days 683 days 80 days 80 days 14 days 900 days 900 days 14 days 900 days 14 days 15 days 16 days 17 days 18 days 18 days 17 days 17 days 18 days 18 days 18 days 18 days 18 days 19 days 10 days	HGC - matholes & ducting construction works (near RW2) HGC - matholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - Aversion & changing over PCCW - diversion & changing construction works (near RW1) PCCW - matholes & ducting construction works (near RW2) PCCW - diversion & changing over (local cables) PCCW - diversion of connection points WSD - pipes frabrication, installation & laying (near RW2) WSD - pipes frabrication installation & laying (near RW2) WSD - swabling flashing/sertilization WSD - swabling/flashing/sertilization
92 90,007 97,100 97,100 97,100 98,100 98,100 100,100 1	Wed 13 May 12 Mm 13 Aer 1 Wed 13 May 12 Wed 13 May 14 Wed 13 May 14 Wed 13 May 1 The 12 May 22 Sir 12 New 22 Sir 12 Dec 1 Sir 12 Dec 1 Sir 12 Dec 2 Sir 12 Dec 3 Sir 12 Dec 5 Wed 12 Dec 5	60 days 60 days 10 days 80 days 11 days 90 days 90 days 90 days 90 days 12 days 12 days 12 days 12 days 12 days 12 days 13 days 14 days 15 days 16 days 17 days 17 days 17 days 18 days 19 days 19 days 19 days 19 days 19 days	HGC - manholes & ducting construction works (near RW2) HGC - manholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - APPORT of the changing over PCCW - APPORT of the changing over PCCW - manholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW2) PCCW - diversion & changing over (local cables) PCCW - diversion of changing over (local cables) PCCW - diversion of connection points with WSD WSD - injection of connection points with WSD WSD - washing flushing startifization WSD - subdising 4 scomissioning by WSD WSD - diversion of 3 mos. din 25 pipes Remaining bas cabried Construction of by side of box culvert for East Round Construction of by side of box culvert for East Round Construction of by side of box culvert for East Round
92. 90.007 93.101 97.101 97.102 98.102 98.107 100.107 100.107 100.107 101 101 101 101 101 101 101 101 101	Wed 13 May 12 Mnn 13 Aer 1 Wed 13 May 14 Mnn 12 May 16 Eri 13 Mn 18 Wed 13 Mny 1 Wed 13 Mny 1 Mnn 12 Mny 22 Thu 12 Mny 22 Sai 12 Nny 22 Sai 12	Oldoss Ol	HGC - manholes & ducting construction works (near RW2) HGC - manholes & ducting construction works (near RW2) HGC - diversion & charging over PCCW - APP application PCCW - Table & charging over PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - diversion & charging per ore (local analous) PCCW - diversion & charging per ore (local analous) PCCW - diversion & charging per ore (local analous) PCCW - diversion & charging per ore (local analous) PCCW - diversion & charging per ore (local analous) PCCW - diversion & charging per ore (local analous) PCCW - diversion & charging per ore (local analous) PCCW - diversion of construction per manholes above (locar RW1) WSD - pipes frainfraiton, installation & laying (near RW2) WSD - pipes frainfraiton, installation & laying (near RW2) WSD - pipes frainfraiton, installation with WSD WSD - inspection of connection points WSD - diversion of connection points WSD - temporal of disused piped reinstaltement WSD - diversion of 3 nos. dia.25 pipes Remaining box calvets WSD - diversion of 3 nos. dia.25 pipes
92 90,007 91,101 92,100 95,102 96,000 96 97,100,100 100,10	Wed 13 May 12 Men 13 Aer 1 Wed 15 Jan 12 Men 12 May 14 Men 12 May 14 Men 12 May 14 Wed 13 May 1 Wed 13 May 1 Wed 13 May 1 Men 12 May 1 Men 12 May 1 Men 13 May 2 The 12 May 2	90 days 60 days 60 days 60 days 60 days 60 days 90 day	HGC - matholes & ducting construction works (near RW1) HGC - matholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - MCCW - AP application PCCW - Anniholes & ducting construction works (near RW1) PCCW - matholes & ducting construction works (near RW1) PCCW - diversion & changing over (local cables) PCCW - diversion & changing over (loversea cables - about 4 nes.) - to be hanged up for construction of remaining Bas Culvert WSD - material delivery WSD - pairs frainfraiden, installation & laying (near RW2) WSD - pairs frainfraiden, installation & laying (near RW2) WSD - tecavation of connection points with WSD WSD - shutdown & commissioning by WSD WSD - shutdown & commissioning by WSD WSD - tecavoral of disset appear fraintatment WSD - temporal of dissets of pipes fraintatment WSD - temporal of dissets of pipes fraintatment
92 90,977 91,101 92,100 95,102 96,00 96,00 96,00 97,100 97,100 97,100 97,100 97,100 98,100 98,100 100,	Wed 13 May 12 Mm 13 Aer 1 Wed 15 Jan 12 Mm 12 May 14 Mm 12 May 14 Mm 12 May 14 Wed 13 May 1 Wed 13 May 1 Wed 13 May 1 Wed 13 May 1 Mm 12 May 14 Mm 12 May 14 Mm 13 Jan 18 Fei 13 Jan 19 Wed 13 May 12 The 12 May 22 Sat 12 New 25 The 12 New 15 The 12 New 25	90 days 60 days 60 days 60 days 60 days 60 days 90 days 90 days 90 days 90 days 90 days 12 days 12 days 13 days 14 days 16 days 17 days 18 days 18 days 18 days 18 days 18 days 19 days 10 days	HGC - matholes & ducting construction works (near RW2) HGC - matholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - Machies & ducting construction works (near RW2) PCCW - matholes & ducting construction works (near RW1) PCCW - matholes & ducting construction works (near RW2) PCCW - diversion & changing over (ocal cables) PCCW - diversion & changing over (oversus cables - about 4 nos.) - to be hanged up for construction of remaining Bus Culvert WSD - pulser frabrication, installation & laying (near RW2) WSD - pulser flabrication, installation & laying (near RW2) WSD - pulser flabrication, installation & laying (near RW2) WSD - pulse flabrication, installation with WSD WSD - seawardian of connection points WSD - swabling flabring / sertification WSD - swabling flabring / sertification WSD - shutdown & commissioning by WSD
92 90,007 97,101 97,101 97,102 98,102 98,102 100,107 101 101 101 101 101 101 101 101 101	Wed 13 May 22 Mnn 13 Aer 1 Wed 13 Jan 12 Mnn 12 May 14 Men 12 May 14 Men 12 May 14 Wed 13 May 1 Wed 13 May 1 Wed 13 May 1 Mnn 12 May 14 Mnn 12 May 14 Mnn 12 May 14 Mnn 13 May 11 Mnn 12 May 10 Mnn 12 May 12 Mnn 12 May 22 Mnn 12 Mny 22 Mnn 12	80 days 60 days 10 days 80 days 10 days 11 days 12 days 17 days 17 days 11 days 11 days 11 days 11 days	HGC - matholes & ducting construction works (near RW1) HGC - matholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - Particular Acting to construction works (near RW1) PCCW - Amphiliation PCCW - Amphiliation PCCW - matholes & ducting construction works (near RW1) PCCW - matholes & ducting construction works (near RW2) PCCW - diversion & changing over (local cables) PCCW - matholes & ducting construction works (near RW2) PCCW - matholes & ducting construction & laying (near RW2) WSD - pripes frabrication, installation & laying (near RW2) WSD - pripes frabrication of remaining bas (Cables) WSD - pripes frabrication of connection points WSD - swabling / flashing/ sectilization WSD - swabling/ flashing/ sectilization
92 90,007 97,101 97,100 98,100 98 98 98 98 98 98 98 98 98 98 98 98 98	Wed 13 May 12 Mnn 13 Aer 1 Wed 13 Jan 12 Mnn 12 May 14 Mnn 12 May 14 Mnn 12 May 1 Wed 13 May 1 Wed 13 May 1 Mnn 12 May 14 Mnn 12 May 12 Mnn 12 Mny 12 Mnn 13 Mny 12 Mnn 13 Mny 12 Tao 12 Mny 22 Sai 12 Nny 2 Sai 12 Nny 2 Sai 12 Nny 2 Tao 12 Mny	68 days 68 days 70 days 80 days 10 days 90 days 90 days 90 days 14 days 90 days 16 days 16 days 17 days 17 days 17 days	HGC - manholes & ducting construction works (near RW2) HGC - manholes & ducting construction works (near RW2) HGC - diversion & charging over PCCW - APP application PCCW - manholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - diversion & charging over (local cables) PCCW - diversion & charging over (loversia cables) PCC
92 90,97 91,101 92,102 95,102 95,102 96 97,103 97,1	Wed 13 May 12 Mnn 13 Arr 1 Mnn 12 May 14 Mnn 12 May 14 Mnn 12 May 14 Mnn 13 May 1 Mnn 13 May 14 Mnn 13 May 15 Eri 13 Mny 1 Tha 12 May 22 The 12 May 22 The 12 May 22 The 12 May 22 The 12 May 23 Lat 12 New 3 Lat 12 New 15 Lat 12 New	80 days 60 days 60 days 60 days 21 days 90 days 90 days 90 days 14 days 90 days 15 days 17 days	HGC - matholes & ducting construction works (near RW1) HGC - matholes & ducting construction works (near RW2) HGC - diversion & charging over PCCW - Manables & ducting construction works (near RW2) PCCW - manables & ducting construction works (near RW2) PCCW - manables & ducting construction works (near RW2) PCCW - diversion & charging over (local cables) PCCW - diversion & charging over (loversion about 4 nos.) - to be hanged up for construction of remaining Box Culvert WSD - pipes frabrication, installation & laying (near RW1) WSD - pipes frabrication, installation & laying (near RW2) WSD - cavarion of connection points
92 90,97 91,101 95,102 95,102 96 97 100,107 101 105 106	wed 13 May 12 Men 13 Aer 1 Wed 13 Jan 12 Men 12 May 14 Men 12 May 14 Men 13 May 14 Wed 13 May 14 Wed 13 May 14 Wed 13 May 14 Men 12 May 15 Men 15 May 17 Ton 12 May 2	90 days 463 days 60 days 10 days 21 days 21 days 22 days 390 days	HGC - manholes & ducting construction works (near RW2) HGC - manholes & ducting construction works (near RW2) HGC - dwinslon & changing over PCCW PCCW - Application PCCW - anaholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW1) PCCW - dwinston & changing over (local cables)
92 90,977 91,101 92,102 95,102 96,102 100,107	wed 13 May 12 Mm 13 Aer 1 Wed 15 Jan 12 Mm 12 May 14 Mm 12 May 14 Mm 12 May 14 Wed 13 May 14 Wed 13 May 14 Wed 13 May 12 John 12 May 14 Mm 12 May 14 Mm 12 Jan 18 Wed 13 May 12 Ton 12 May 2 The 12 May 2 The 12 May 2 The 12 May 2	90 days 463 days 60 days 20 days 21 days 22 days 900 days 900 days 900 days 900 days 183 days 48 days 348 days 241 days	HGC - matholes & ducting construction works (near RW1) HGC - matholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - A pepileation PCCW - A papileation PCCW - manholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW1) PCCW - diversion & changing over (near RW2) PCCW - matholes & changing over (near RW2) PCCW - matholes & changing over (near RW2) PCCW - matholes & ducting construction works (near RW2) PCCW - matholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting construction works (near RW2) PCCW - manholes & ducting constructi
92 90,977 91,101 95,102 95,102 96,102 100,107 101,107 101,107	Wed 13 May 12 Med 15 Aur 1 Wed 15 Jan 12 Men 12 May 14 Men 12 May 14 Wed 15 May 14 Wed 15 May 14 Wed 15 May 14 Men 12 May 14 Men 12 May 14 Men 12 May 14 Men 12 May 14 Men 13 May 14 Men 13 May 14 Men 13 May 14 Wed	90 days 463 days 60 days 21 days 21 days 24 days 90 days 900 days	HGC - matholes & ducting construction works (near RW2) HGC - matholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW PCCW - XP application PCCW - anaholes & ducting construction works (near RW1) PCCW - matholes & ducting construction works (near RW2) PCCW - diversion & changing over (local cables)
92 90,977 91.00 92.100 92.100 93.100 94 100.105 100.107	Wed 13 May 12 Men 13 Aer 1 Wed 15 Jan 12 Wed 15 Jan 12 Men 12 May 14 Men 12 May 14 Wed 13 May 1 Wed 13 May 1 Men 12 May 14 Men 12 May 14 Men 12 May 14 Men 13 May 12 Men 13 May 14 Men 13 May 16 Men 13 May 16 Men 13 May 16 Men 13 May 17 Wed 13 May 1	90 days 463 days 60 days 21 days 21 days 900 days	HGC - manholes & ducting construction works (near RW1) HGC - manholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - Manholes & ducting construction works (near RW1) PCCW - annholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW2) PCCW - diversion & changing over (local cables)
92 90,97 91,101 97,101 98,102 98 102,105 100,107 101 101 101 101 101 101 101 101	Wed 13 Mey 22 Wed 13 Mey 14 Wed 13 Mey 14 Men 12 Mey 14 Men 13 Mey 14 Men 13 Mey 12 Men 13 Mey 12 Men 13 Mey 12 Men 13 Mey 14 Men 13 Mey 14 Men 13 Mey 14 Men 13 Mey 14 Men 13 Mey 18 Men 13 Mey 18 Men 13 Mey 18 Men 13 Mey 18	90 days 463 days 60 days 21 days 21 days 20 days 900 days 900 days 60 days 60 days 80 days	HGC - manholes & ducting construction works (near RW1) HGC - manholes & quering construction works (near RW2) HGC - diversion & changing over PCCW PCCW - XP application PCCW - anaholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW2) PCCW - diversion & changing over (local cables)
92 90,97 91,101 97,101 98,102 98 100,107	Wed 13 May 22 Mnn 13 Apr 1 Wed 13 Jan 12 Wed 13 Jan 12 Men 12 May 14 Men 13 May 14 Men 13 May 1 Men 13 May 1 Men 13 May 2 Men 13 May 2 Men 12 May 14 Men 13 May 18 Fei 13 Jan 18	90 days 463 days 60 days 21 days 14 days 90 days 90 days 50 days 90 days	HGC - manholes & ducting construction works (near RW1) HGC - manholes & quiring construction works (near RW2) HGC - diversion & changing over PCCW PCCW - XP application PCCW - anaholes & ducting construction works (near RW1) PCCW - manholes & ducting construction works (near RW2)
92 90.97 91 91,00 95,002 96 100,107	Wed 13 May 22 Mon 13 Apr 1 Wed 13 Jan 12 Wed 13 Jan 12 Wed 13 May 14 Mon 12 May 14 Wed 13 May 1 Mon 13 Mar 18 Wed 13 May 1 Mon 13 Mar 18 Mon 12 May 14 Mon 12 May 14 Mon 13 Mar 18	90 days 463 days 60 days 21 days 21 days 90 days 90 days 900 days 60 days	HGC - manholes & ducting construction works (near RW1) HGC - manholes & ducting construction works (near RW2) HGC - diversion & changing over PCCW - Application PCCW - Application PCCW - manholists & ducting construction works (near RW1)
92 90,01 91,01 97,101 97,101 97,101 102,105 102,105 101	Wed 13 May 22 Mon 13 Apr 1 Wed 13 Jun 12 Wed 13 Jun 12 Wed 13 May 14 Mon 12 May 14 Wed 13 May 14 Wed 13 May 18 Wed 13 May 12 Mon 12 May 14	90 days 463 days 60 days 21 days 21 days 900 days	HGC - manholes & ducting construction works (near RVV)) HGC - manholes & ducting construction works (near RV2) HGC - ductsion & changing over PCVP PCVP
92 90,007 91 91 92.100 95.100 96 100.100 100.100	Wed 13 May 22 Mnn 13 Apr 1 Wed 13 Jun 12 Mnn 12 May 14 Wed 13 May 1 Wed 13 May 1 Mon 13 Mar 18	90 days 463 days 60 days 21 days 14 days 90 days	HGC - manholes & duxting construction works (near RW1) HGC - manholes & duxting construction works (near RW2) HGC - diversion & changing over
92 90,977 91 91 92,100 95,102 95,102 96 96	Wed 13 May 22 Mon 13 Apr 1 Wed 13 Jun 12 Mon 12 May 14 Mon 12 May 14 Wed 13 May 1 Mon 13 Mar 18	90 days 463 days 60 days 21 days 14 days	HGC - manholes & ducting construction works (near RW1) HGC - manholes & ducting construction works (near RW2)
92 90,97 91,101 97,101 98,102 98,102	Wed 13 May 22 Mnn 13 Apr 1 Wed 13 Jun 12 Mion 12 May 14 Mnn 12 May 14 Wed 13 May 1	90 days 463 days 60 days 21 days	HGC - manholes & ductine construction works (near RW1)
92 90,97 91 97,101 98,102	Wed 13 May 22 Mnn 13 Apr 1 Wed 13 Jan 12 Mon 12 May 14	90 days 463 days	and the officers of
92 90.97 91 91,101 95,102	Wed 13 May 22 Mnn 13 Apr 1 Wed 13 Jun 12	90 days	HGC - XP application
92 90,997 91 91,101 95,102	Wed 13 May 22 Mnn 13 Apr 1		NWT - diversion & changing over
92 90,97 91,101	Wed 13 May 22	14 days	NWT - munholes & ducting construction works (near RW2)
92 90,97		21 days	NWT - manholes & ducting construction works (near RW1)
92 90,97 91	Mon 12 May 14	60 days	NWT - XP application
92 90,97	Mon 12 May 14	484 days	NWI
92	Mon 13 Apr 15	21 days	CLP (2 no. 11kV cables) - ducting & cable works (near KW2)
	Mon 13 May 6	21 days	CLP (2 no. 11kV cables) - ducting & cable works (near RW1)
Time to fell to	Mon 12 May 14	60 days	CLP (2 no. 11kV cables) - XP application
Sm 13 m 10.	Mon 12 May 14	399 days	CLP (2no. 11kV cables)
	Fri 12 Jul 20	60 days	Retaining wall RW2 (wing wall)
Tau 12 Jul 19 85	Fri 12 Jul 13	7 days	PCCW - demolition of existing joint box/ cable drawpit
Thu 12 M 12	Mon 12 May 14	60 days	PCCW - XP application
wallow 82	Sat 12 Sep 1	127 days	Retaining wall RWI - wing wall portion
Fri 12 Aug 31 81	Sat 12 Aug 25	7 days	CLP (overhead pole) - removal of overhead pole
Fri 12 Aug 24 80	Sat 12 Aug 11	14 days	CLP (overhead pole) - changing over
FILZARIO 78	Mon 12 May 28	75 days	CLP (everhead pole) - cable laying
	W- 17 W- 70		Bound)
Mm 12 Ar 16 76	Sat 12 Apr 14	3 days	Remove Temporary flow diversion Construction of 3 5m wide to also of box cultured along Costle Book Road (East
Fi 12 Apr 13 7 5	Thu 12 Mar 15	30 days	Construction of Base Slab & Wall of Box Culvert along Castle Peak Road (Last Bound)
	Mon 12 Mar 12	3 days	Demolish Existing Box Culvert (East Bound)
	Mon 12 Mar 5	7 days	Temporary support for utilities
	Tue 12 Feb 28	6 days	Installation of steel sheet piles
	Tue 12 Feb 21	7 days	Trial pit for utilities Construction of steel footbadge
	Mon 12 Feb 20	1 day	Implement Stage 3 of TTA
2	Wed 12 Ian 18	33 days	demolition of ex. BC
2 Jan 17	Tur 11 Doc 6	43 days	onstruction of Box Culvert along Castle Peak Road (West Bound) including
Finish Predecessors (1 2011, Half 2 2012, Half 1 2012, Half 2 2013, Half 1 2014, Half 2 2014, Half	Start	Duration	Task Name

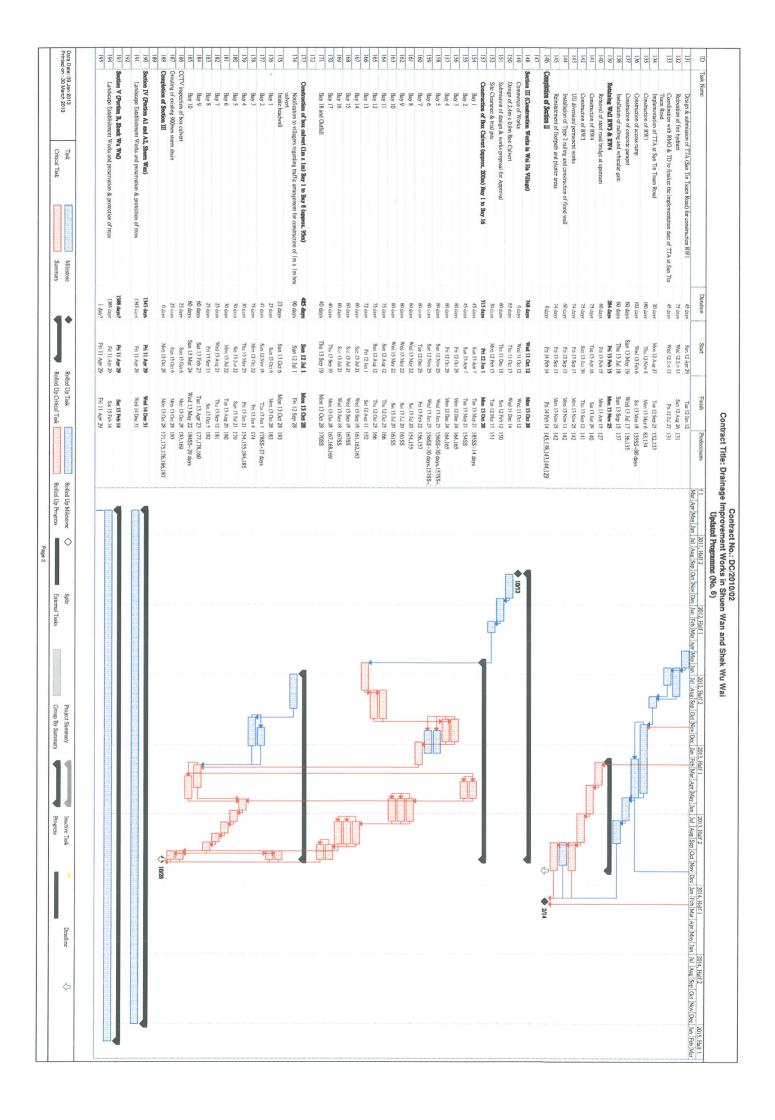

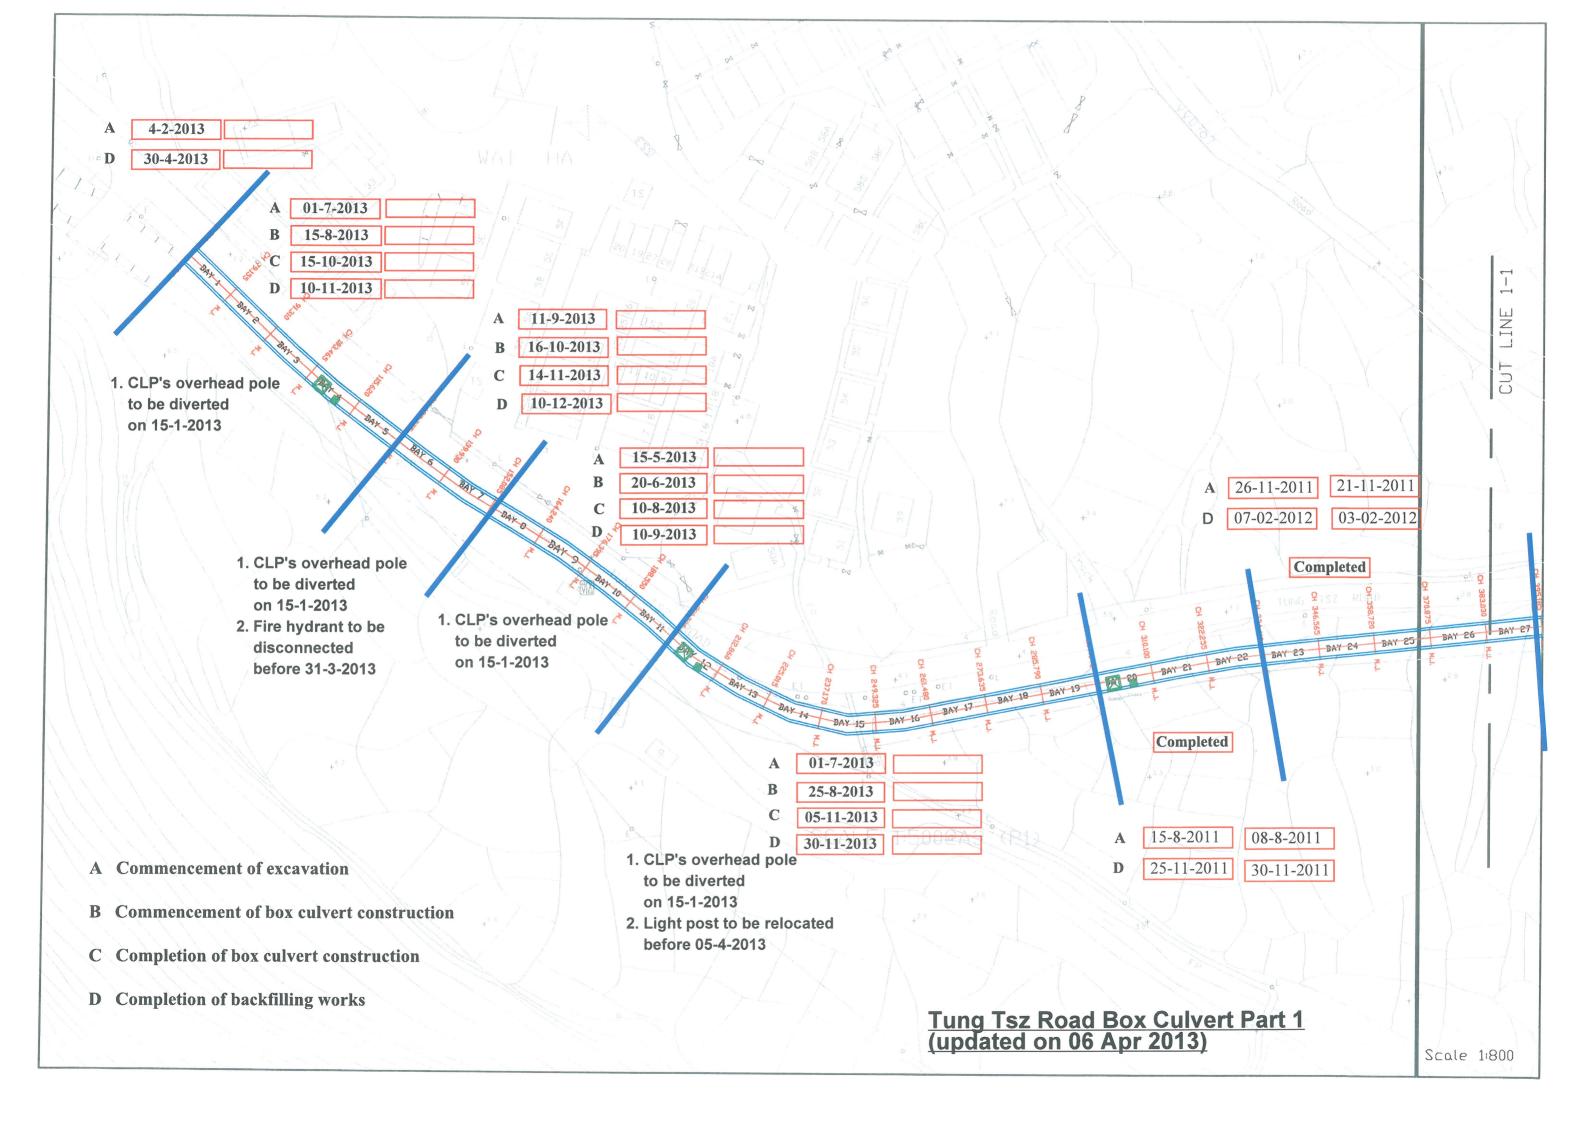

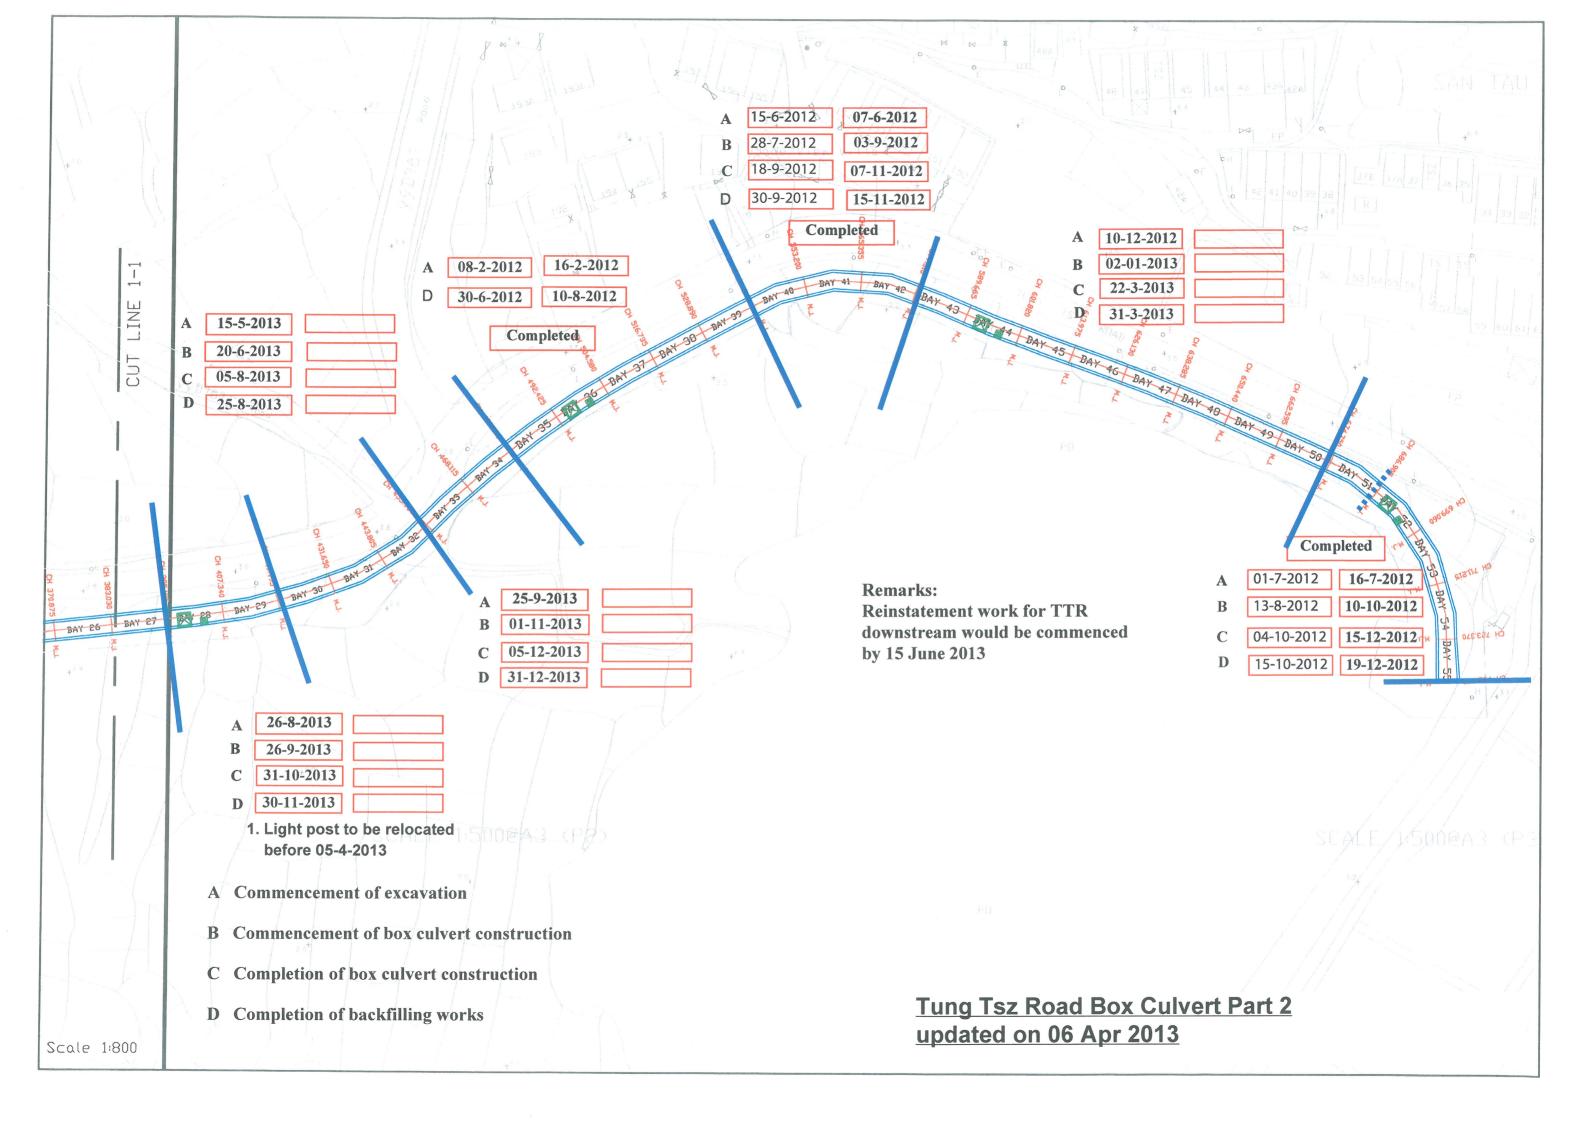


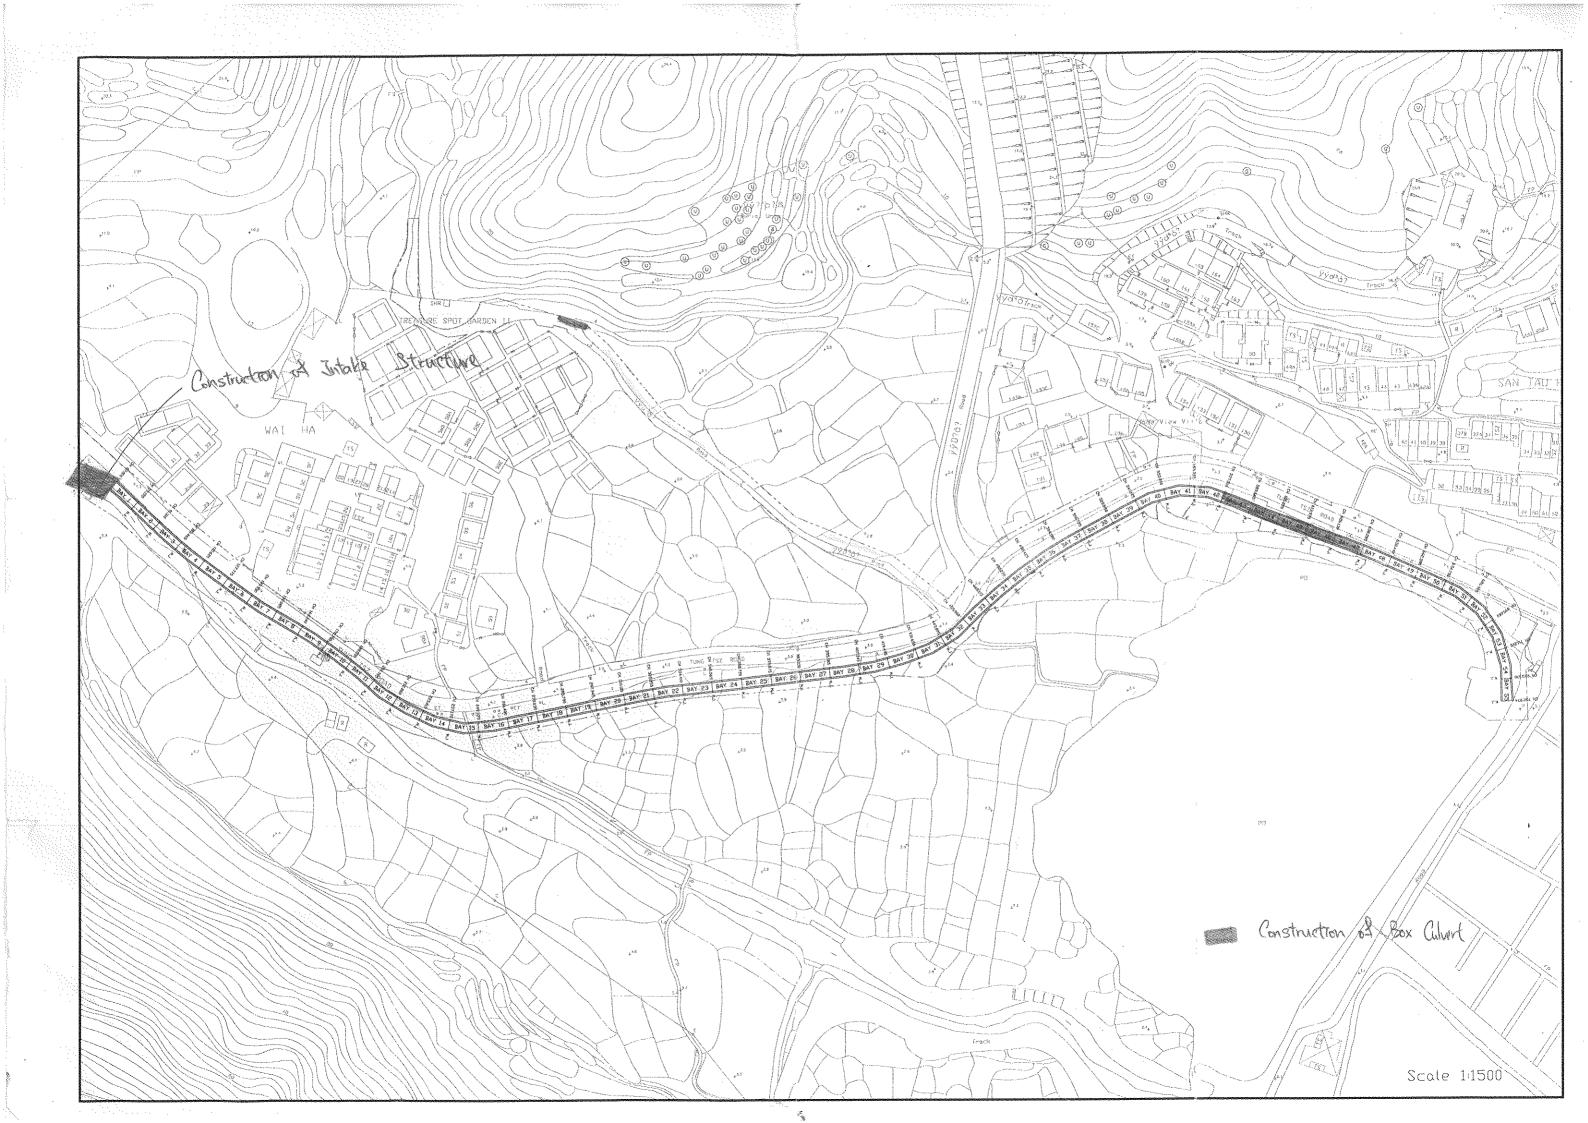



Appendix D

Environmental Monitoring Locations

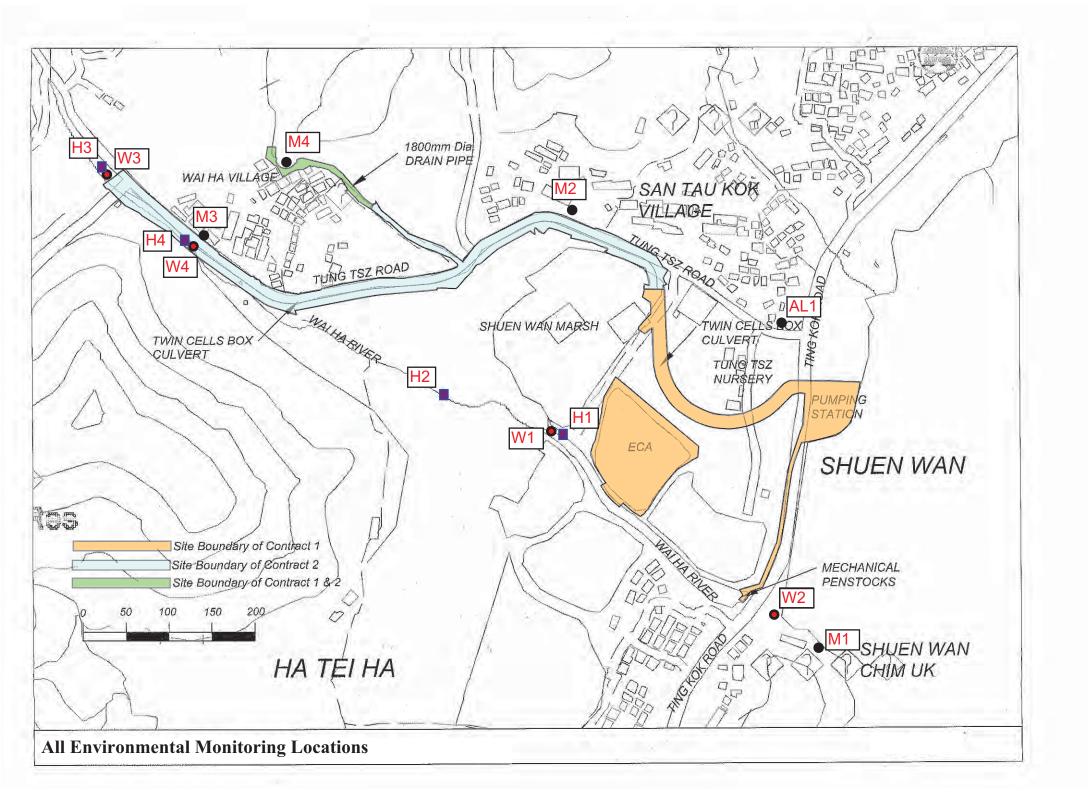



Appendix E

Calibration certificates of the monitoring equipment and Certificate of ALS Technichem (HK) Pty Ltd



Equipment Calibration List

Items	Aspect	Description of Equipment	Date of Calibration	Date of Next Calibration
1*	N	Bruel & Kjaer Integrating Sound Level Meter (Serial No. 2337676)	18 May 13	18 May 13
2*	Noise	Bruel & Kjaer Acoustical Calibrator (Serial No. 2326408)	7 May 13	7 May 13
3		HACH Turbidmeter 2100Q (Serial No.11030C008499)	14 Jan 13	14 Apr 13
4*	***	SONDA YSI 6820 (Serial No. 02J0912)	16 Apr 13	16 Jul 13
5	Water	DO Meter YSI Pro 20 (Serial No. 12C100570)	8 Jan 13	8 Apr 13
6*		YSI 550A (Serial No. 05F2063AZ)	8 Apr 13	8 Jul 13

Note: *Calibration certificates will only be provided when monitoring equipment is re-calibrated or new.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C123007

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC12-0960)

Description / 儀器名稱

Integrating Sound Level Meter (EQ065)

Manufacturer / 製造商

Bruel & Kjaer

Model No. / 型號

2238

Serial No. / 編號

2337676

Supplied By / 委託者 Action-United Environmental Services and Consulting

> Unit A, 20/F., Gold King Industrial Building, 35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 :

Relative Humidity / 相對濕度 :

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

18 May 2012

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

All results are within manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

K/C/Lee

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Precision Measurement Ltd., UK
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By

測試

Certified By

Date of Issue 簽發日期

22 May 2012

核證 C Cheung

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior

written approval of this laboratory 本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗所

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C123007

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

2. Self-calibration using laboratory acoustic calibrator was performed before the test from 6.1.1.2 to 6.4.

3. The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment:

Equipment ID

Description

Certificate No.

CL280

40 MHz Arbitrary Waveform Generator

C120016

CL281

Multifunction Acoustic Calibrator

DC110233

5. Test procedure: MA101N.

6. Results:

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

6.1.1.1 Before Self-calibration

UUT Setting				Applied Value		UUT	
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	
50 - 130	LAFP	A	F	94.00	1	94.3	

6.1.1.2 After Self-calibration

	UUT	Setting		Applied	d Value	UUT	IEC 60651
Range	Parameter	Frequency	Time	Level	Freq.	Reading	Type 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
50 - 130	L_{AFP}	A	F	94.00	1	94.1	± 0.7

6.1.2 Linearity

	UU	Γ Setting	Applie	d Value	UUT	
Range	Parameter	Frequency	Time	Level	Freq.	Reading
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)
50 - 130	L _{AFP}	A	F	94.00	1	94.1 (Ref.)
				104.00		104.1
8				114.00		114.1

IEC 60651 Type 1 Spec. : \pm 0.4 dB per 10 dB step and \pm 0.7 dB for overall different.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C123007

證書編號

6.2 Time Weighting

Continuous Signal 6.2.1

Continuous	Continuous Signar						
		Applied Value		UUT	IEC 60651		
Range	Parameter	Frequency	Time	Level	Freq.	Reading	Type 1 Spec.
(dB)	,	Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
50 - 130	L _{AFP}	A	F	94.00	1	94.1	Ref.
	L _{ASP}	-	S			94.1	± 0.1
	LAIP		I		>	94.1	± 0.1

Tone Burst Signal (2 kHz) 6.2.2

	UUT	Setting		Applied Value		UUT	IEC 60651
Range	Parameter	Frequency	Time	Level	Level Burst		Type 1 Spec.
(dB)		Weighting	Weighting	(dB)	Duration	(dB)	(dB)
30 - 110	L _{AFP}	A	F	106.0	Continuous	106.0	Ref.
	L _{AFMax}				200 ms	105.1	-1.0 ± 1.0
	L _{ASP}		S		Continuous	106.0	Ref.
	L _{ASMax}				500 ms	102.0	-4.1 ± 1.0

6.3 Frequency Weighting

6.3.1 A-Weighting

	UUT	Setting		Applied Value		UUT	IEC 60651
Range	Parameter	Frequency	Time	Level	Freq.	Reading	Type 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
50 - 130	L_{AFP}	A	F	94.00	31.5 Hz	55.0	-39.4 ± 1.5
	#630000003				63 Hz	68.0	-26.2 ± 1.5
					125 Hz	78.0	-16.1 ± 1.0
					250 Hz	85.4	-8.6 ± 1.0
					500 Hz	90.8	-3.2 ± 1.0
	541.				1 kHz	94.1	Ref.
			×		2 kHz	95.3	$+1.2 \pm 1.0$
					4 kHz	95.1	$+1.0 \pm 1.0$
				3	8 kHz	93.0	-1.1 (+1.5; -3.0)
			7		12.5 kHz	89.9	-4.3 (+3.0 ; -6.0)

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration

校正證書

Certificate No.:

C123007

證書編號

6.3.2 C-Weighting

	UUT	Setting		Applie	ed Value	UUT	IEC 60651
Range	Parameter	Frequency	Time	Level	Freq.	Reading	Type 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
50 - 130	L_{CFP}	С	F	94.00	31.5 Hz	91.3	-3.0 ± 1.5
	-				63 Hz	93.3	-0.8 ± 1.5
					125 Hz	93.9	-0.2 ± 1.0
					250 Hz	94.0	0.0 ± 1.0
			٠		500 Hz	94.1	0.0 ± 1.0
	,				1 kHz	94.1	Ref.
					2 kHz	93.9	-0.2 ± 1.0
	,				4 kHz	93.2	-0.8 ± 1.0
					8 kHz	91.1	-3.0 (+1.5 ; -3.0)
			-		12.5 kHz	88.0	-6.2 (+3.0 ; -6.0)

6.4 Time Averaging

	UUT	Setting		Applied Value				UUT	IEC 60804	
Range	Parameter	Frequency	Integrating	Frequency	Burst	Burst	Burst	Equivalent	Reading	Type 1
(dB)		Weighting	Time	(kHz)	Duration	Duty	Level	Level	(dB)	Spec.
				2 2	(ms)	Factor	(dB)	(dB)		(dB)
30 - 110	L_{Aeq}	A	10 sec.	4	1	1/10	110.0	100	99.9	± 0.5
						1/10 ²	,	90	89.7	± 0.5
	a		60 sec.			1/10 ³		80	79.7	± 1.0
			5 min.			1/104		70	69.7	± 1.0

Remarks: - Mfr's Spec.: IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value : 94 dB : $31.5 \, \text{Hz} - 125 \, \text{Hz}$: $\pm 0.35 \, \text{dB}$

250 Hz - 500 Hz : ± 0.30 dB 1 kHz : ± 0.20 dB 2 kHz - 4 kHz : ± 0.35 dB 8 kHz : ± 0.45 dB

8 kHz : $\pm 0.45 \text{ dB}$ 12.5 kHz : $\pm 0.70 \text{ dB}$

 $104 \, dB : 1 \, kHz$: $\pm 0.10 \, dB \, (Ref. 94 \, dB)$ $114 \, dB : 1 \, kHz$: $\pm 0.10 \, dB \, (Ref. 94 \, dB)$ Burst equivalent level : $\pm 0.2 \, dB \, (Ref. 110 \, dB)$

continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

Note:

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗所



ALS Technichem (HK) Pty Ltd

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:

MR BEN TAM

CLIENT:

ACTION UNITED ENVIRO SERVICES

ADDRESS:

RM A 20/F., GOLDEN KING IND BLDG. NO. 35-41 TAI LIN PAI ROAD,

KWAI CHUNG,

N.T., HONG KONG

PROJECT:

WORK ORDER:

HK1309651

LABORATORY: DATE RECEIVED: HONG KONG 11/04/2013

DATE OF ISSUE:

17/04/2013

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal aceptance criteria of ALS will be followed.

Scope of Test:

Dissolved Oxygen, Turbidity, pH, Salinity and Temperature

Equipment Type:

SONDE

Brand Name:

YSI

Model No.: Serial No.:

YSI 6820 / 650MDS 02J0912/02K0788 AA

Equipment No.:

Date of Calibration: 16 April, 2013

NOTES

This is the Final Report and supersedes any preliminary report with this batch number. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ISSUING LABORATORY: HONG KONG

Address

ALS Technichem (HK) Pty Ltd

11/F Chung Shun Knitting Centre

1-3 Wing Yip Street

Kwai Chung HONG KONG Phone:

852-2610 1044

Fax:

852-2610 2021

Email:

hongkong@alsglobal.com

Mr. Fung Lim Chee

General Manager

Greater China & Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

Page 1 of 2

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order:

HK1309651

Date of Issue:

17/04/2013

Client:

ACTION UNITED ENVIRO SERVICES



Equipment Type:

SONDE

Brand Name:

YSI

Model No.: Serial No.: YSI 6820 / 650MDS 02J0912/02K0788 AA

Equipment No.:

Date of Calibration:

16 April, 2013

Date of next Calibration:

16 July, 2013

Parameters:

Dissolved Oxygen

Method Ref: APHA (21st edition), 45000: G

	Method Ren / H Thr (215t curti	Method Ren 7 ti 11/7 (2250 edition), 150001 d								
Î	Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)							
			-							
	5.51	7.86	2.35							
	8.65	8.66	0.01							
	14									
		Tolerance Limit (±mg/L)	0.20							

pH Value

Method Ref: APHA 21st Ed. 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	3.98	-0.02
7.0	6.92	-0.08
10.0	9.97	-0.03
	Tolerance Limit (±pH unit)	0.20

Salinity

Method Ref: APHA (21st edition), 2520B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)		
0	0.08			
10	10.83	8.3		
20	21.15	5.7		
30	32.28	7.6		
	Tolerance Limit (±%)	10.0		

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
12.0	11.40	0.6
12.0	11.40	-0.6
23.0	22.54	-0.5
42.5	42.68	0.2
	Tolerance Limit (±°C)	2.0

Turbidity

Method Ref: APHA (21st edition), 2130B

Method Ref. AFHA (21st edition), 21508					
Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)			
0	-0.2				
40	42.6	6.5			
80	78.0	-2.5			
400	435.5	8.9			
800	782.9	-2.1			
	Tolerance Limit (±%)	10.0			

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr. Fung Lim Chee, Richard General Manager -

Greater China & Hong Kong

ALS Technichem (HK) Pty Ltd

ALS Environmental



ALS Technichem (HK) Pty Ltd

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:

MR BEN TAM

CLIENT: ADDRESS: **ACTION UNITED ENVIRO SERVICES** RM A 20/F., GOLDEN KING IND BLDG,

NO. 35-41 TAI LIN PAI ROAD,

KWAI CHUNG. N.T., HONG KONG

PROJECT:

WORK ORDER:

HK1309162

LABORATORY:

HONG KONG

DATE RECEIVED:

08/04/2013

DATE OF ISSUE:

17/04/2013

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal aceptance criteria of ALS will be followed.

Scope of Test:

Dissolved Oxygen and Temperature

Equipment Type:

Multimeter

Brand Name: Model No.:

YSI

Serial No.:

YSI 550A 05F2063AZ

Equipment No.:

Date of Calibration: 08 April, 2013

NOTES

This is the Final Report and supersedes any preliminary report with this batch number. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ISSUING LABORATORY: HONG KONG

Address

ALS Technichem (HK) Pty Ltd

11/F Chung Shun Knitting Centre

1-3 Wing Yip Street

Kwai Chung HONG KONG Phone:

852-2610 1044

Fax:

852-2610 2021

Email:

hongkong@alsglobal.com

Mr. Fung Lim Chee

General Manager -

Greater China & Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

Page 1 of 2

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order:

HK1309162

Date of Issue:

17/04/2013

Client:

ACTION UNITED ENVIRO SERVICES



Description:

Multimeter

Brand Name:

YSI

Model No.:

YSI 550A 05F2063AZ

Serial No.: Equipment No.:

0.5

Date of Calibration:

08 April, 2013

Date of next Calibration:

08 July, 2013

Parameters:

Dissolved Oxygen

Method Ref: APHA (21st edition), 45000: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)	
3.19	3.35	0.16	
6.01	6.17	0.16	
8.29	8.38	0.09	
	Tolerance Limit (±mg/L)	0.20	

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical
Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

	Carac Hor 3 Second Cartion March 2000, Working Thermometer Campianon Froduction				
	Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)		
		000000			
-	13.0	13.2	0.2		
-	22.0	22.2	0.2		
	43.4	43.1	-0.3		
		Tolerance Limit (±°C)	2.0		

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr. Fung Lim Chee, Richard General Manager -

Greater China & Hong Kong



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

C122712 Certificate No.:

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC12-0960)

Description / 儀器名稱

Acoustical Calibrator (EQ081)

Manufacturer / 製造商

Bruel & Kjaer

Model No. / 型號 Serial No. / 編號

4231

Supplied By / 委託者

2326408 Action-United Environmental Services and Consulting

Unit A, 20/F., Gold King Industrial Building, 35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度

Relative Humidity / 相對濕度:

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

7 May 2012

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

All results are within manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By 測試

K/C/Lee

Certified By

Date of Issue 簽發日期

8 May 2012

核證

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior

written approval of this laborator 本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗所

co香港新界屯門與安里一號青山灣機樓四樓 Tel/電話: 2927 2606

E-mail/電郵: callab@suncreation.com Fax/傳真: 2744 8986

Website/網址: www.suncreation.com

Page 1 of 2



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C122712

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

The results presented are the mean of 3 measurements at each calibration point. 2.

Test equipment: 3.

> Equipment ID CL130 CL281 TST150A

Certificate No. Description C113350 Universal Counter DC110233 Multifunction Acoustic Calibrator C120886 Measuring Amplifier

4. Test procedure: MA100N.

Results:

Sound Level Accuracy 5.1

July Turn	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
UUT Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.0		

5.2

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Appendix F

Event and Action Plan

DSD Contract No. Contract No. DC/2010/02 - Drainage Improvement in Shuen Wan and Shek Wu Wai

22nd Monthly EM&A Report –April 2013



Event Action Plan for Construction Noise

EVENT		AC	TION	
EVENI	ET Leader	IEC	ER	Contractor
Action Level	 Notify IEC and Contractor Carry out investigation. Report the results of investigation to the IEC, ER and Contractor. Discuss with the Contractor and formulate remedial measures Increase monitoring frequency to check mitigation effectiveness. 	Review the analyzed results submitted by the ET. Review the proposed remedial measures by the Contractor and advise the ER accordingly Supervise the implementation of remedial measures	Confirm receipt of notification of failure in writing Notify Contractor Require Contractor to propose 'remedial measures for the analyzed noise problem Check remedial measures are properly implemented.	Submit noise mitigation proposals to IEC Implement noise mitigation proposals
Limit Level	1. Notify IEC, ER, EPD and Contractor 2. Identify source. 3. Repeat measurements to confirm findings 4. Increase monitoring frequency. 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results 8. If exceedance stops, cease additional monitoring.	Discuss amongst ER, ET, and Contractor on the potential remedial actions Review Contractor's' remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly Supervise the implementation of remedial measures	1. Confirm receipt of notification of failure in writing 2. Notify Contractor 3. Require Contractor to propose remedial measures for the analyzed noise problem 4. Check remedial measures properly implemented. 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated	 Take immediate action to avoid further exceedance Submit proposals for remedial actions to IEC within 3 working days of notification Implement the agreed proposals Resubmit proposals if problem still not under control Stop the relevant portion of works as determined by the ER until the exceedance is abated



Event and action Plan for Water Quality

Event	ET Leader	IEC ACTION LEVEL	ER	Contractor
Action level being exceeded by one sampling day	1. Repeat in-situ measurements to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IEC, Contractor and Engineer; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, Engineer and Contractor; 6. Ensure mitigation measures are implemented. 7. Repeat measurement on next day of exceedance.	1. Discuss mitigation measures with ET, Engineer and Contractor; 2. Review proposals on mitigation measures submitted by Contractor and advise the Engineer accordingly; 3. Assess effectiveness of implemented mitigation measures.	Discuss proposed mitigation measures with IEC, ET and Contractor; Make agreement on mitigation measures to be implemented; Assess effectiveness of implemented mitigation measures.	1. Inform Engineer and confirm in writing notification of the non-compliance; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes in working methods; 5. Discuss with ET, IEC and Engineer and propose mitigation measures to IEC and Engineer within three working days; 6. Implement agreed mitigation measures.
Action level being exceeded by more than two consecutive sampling days	1. Repeat in-situ measurements to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IEC, Contractor and Engineer; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, Engineer and Contractor; 6. Ensure mitigation measures are implemented. 7. Prepare to increase the monitoring frequency to daily; 8. Repeat measurement on next day of exeedance.	Discuss mitigation measures with ET, Engineer and Contractor; Review proposals on mitigation measures submitted by Contractor and advise the Engineer accordingly; Assess effectiveness of implemented mitigation measures.	Discuss proposed mitigation measures with IEC, ET and Contractor; Make agreement on mitigation measures to be implemented; Assess effectiveness of implemented mitigation measures.	Inform Engineer and confirm in writing notification of the non-compliance; Rectify unacceptable practice; Check all plant and equipment; Consider changes in working methods; Discuss with ET, IEC and Engineer and propose mitigation measures to IEC and Engineer within three working days; Implement agreed mitigation measures
Limit level being exceeded by one sampling day	1. Repeat in-situ measurements to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform EPD, IEC, Contractor and Engineer; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, Engineer and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level.	1. Discuss mitigation measures with ET, Engineer and Contractor; 2. Review proposals on mitigation measures submitted by Contractor and advise the Engineer accordingly; 3. Assess effectiveness of implemented mitigation measures.	Discuss proposed mitigation measures with IEC, ET and Contractor; Request Contractor to critically review the working methods; Make agreement on mitigation measures to be implemented; Assess effectiveness of implemented mitigation measures.	1. Inform Engineer and confirm in writing notification of the non-compliance; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes in working methods; 5. Discuss with ET, IEC and Engineer and propose mitigation measures to IEC and Engineer within three working days; 6. Implement agreed mitigation measures.
Limit level being exceeded by more than two consecutive sampling days	1. Repeat in-situ measurements to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform EPD, IEC, Contractor and Engineer; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, Engineer and Contractor; 6. Ensure mitigation measures are implemented. 7. Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.	Discuss mitigation measures with ET, Engineer and Contractor; Review proposals on mitigation measures submitted by Contractor and advise the Engineer accordingly; Assess effectiveness of implemented mitigation measures.	1. Discuss proposed mitigation measures with IEC, ET and Contractor; 2. Request Contractor to critically review the working methods; 3. Make agreement on mitigation measures to be implemented; 4. Assess effectiveness of implemented mitigation measures; 5. Consider and if necessary instruct Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit Level.	1. Inform Engineer and confirm in writing notification of the non-compliance; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes in working methods; 5. Discuss with ET, IEC and Engineer and propose mitigation measures to IEC and Engineer within three working days; 6. Implement agreed mitigation measures; 7. As directed by the Engineer, slow down or stop all or part of the construction activities until no exceedance of Limit level.



Event and action Plan for Hydrological Characteristics

Event ACTION LEVEL	ET Leader	IEC	ER	Contractor
Action level being exceeded by one sampling day	1. Repeat in-situ measurements to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IEC, Contractor and Engineer; 4. Check monitoring data, Contractor's working methods and any excavation works or dewatering processes; 5. Discuss mitigation measures with IEC, Engineer and Contractor; 6. Ensure mitigation measures are implemented. 7. Repeat measurement on next day of exceedance.	Discuss mitigation measures with ET, Engineer and Contractor; Review proposals on mitigation measures submitted by Contractor and advise the Engineer accordingly; Assess effectiveness of implemented mitigation measures.	Discuss proposed mitigation measures with IEC, ET and Contractor; Make agreement on mitigation measures to be implemented; Assess effectiveness of implemented mitigation measures.	1. Inform Engineer and confirm in writing notification of the non-compliance; 2. Rectify unacceptable practice; 3. Check working methods and any excavation works or dewatering processes; 4. Consider changes in working methods and plans; 5. Discuss with ET, IEC and Engineer and propose mitigation measures to IEC and Engineer within three working days; 6. Implement agreed mitigation measures.
Action level being exceeded by more than two consecutive sampling days	1. Repeat in-situ measurements to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform IEC, Contractor and Engineer; 4. Check monitoring data, Contractor's working methods and any excavation works or dewatering processes; 5. Discuss mitigation measures with IEC, Engineer and Contractor; 6. Ensure mitigation measures are implemented. 7. Prepare to increase the monitoring frequency to daily; 8. Repeat measurement on next day of exeedance.	Discuss mitigation measures with ET, Engineer and Contractor; Review proposals on mitigation measures submitted by Contractor and advise the Engineer accordingly; Assess effectiveness of implemented mitigation measures.	Discuss proposed mitigation measures with IEC, ET and Contractor; Make agreement on mitigation measures to be implemented; Assess effectiveness of implemented mitigation measures.	1. Inform Engineer and confirm in writing notification of the non-compliance; 2. Rectify unacceptable practice; 3. Check working methods and any excavation works or dewatering processes; 4. Consider changes in working methods and plans; 5. Discuss with ET, IEC and Engineer and propose mitigation measures to IEC and Engineer within three working days; 6. Implement agreed mitigation measures
Limit level being exceeded by one sampling day	1. Repeat in-situ measurements to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform AFCD, IEC, Contractor and Engineer; 4. Check monitoring data, and Contractor's working methods and any excavation works or dewatering processes; 5. Discuss mitigation measures with IEC, Engineer and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit level.	Discuss mitigation measures with ET, Engineer and Contractor; Review proposals on mitigation measures submitted by Contractor and advise the Engineer accordingly; Assess effectiveness of implemented mitigation measures.	Discuss proposed mitigation measures with IEC, ET and Contractor; Request Contractor to critically review the working methods; Make agreement on mitigation measures to be implemented; A. Assess effectiveness of implemented mitigation measures.	1. Inform Engineer and confirm in writing notification of the non-compliance; 2. Rectify unacceptable practice; 3. Check working methods and any excavation works or dewatering processes; 4. Consider changes in working methods and plans; 5. Discuss with ET, IEC and Engineer and propose mitigation measures to IEC and Engineer within three working days; 6. Implement agreed mitigation measures.
Limit level being exceeded by more than two consecutive sampling days	1. Repeat in-situ measurements to confirm findings; 2. Identify reasons for non-compliance and source(s) of impact; 3. Inform AFCD, IEC, Contractor and Engineer; 4. Check monitoring data and Contractor's working methods and any excavation works or dewatering processes; 5. Discuss mitigation measures with IEC, Engineer and Contractor; 6. Ensure mitigation measures are implemented. 7. Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.	Discuss mitigation measures with ET, Engineer and Contractor; Review proposals on mitigation measures submitted by Contractor and advise the Engineer accordingly; Assess effectiveness of implemented mitigation measures.	1. Discuss proposed mitigation measures with IEC, ET and Contractor; 2. Request Contractor to critically review the working methods; 3. Make agreement on mitigation measures to be implemented; 4. Assess effectiveness of implemented mitigation measures; 5. Consider and if necessary instruct Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit Level.	1. Inform Engineer and confirm in writing notification of the non-compliance; 2. Rectify unacceptable practice; 3. Check working methods and any excavation works or dewatering processes; 4. Consider changes in working methods and plans; 5. Discuss with ET, IEC and Engineer and propose mitigation measures to IEC and Engineer within three working days; 6. Implement agreed mitigation measures; 7. As directed by the Engineer, slow down or stop all or part of the construction activities until no exceedance of Limit level.



Appendix G

Monitoring Schedule in Reporting Period and the Coming Month



Monitoring Schedule in this Reporting Period – April 2013

Г	Date Stream Monitoring Noise Monitor			
L	Jaile	Water Sampling	Flow Monitoring	Noise Mointoinig
Mon	1-Apr-13			
Tue	2-Apr-13			
Wed	3-Apr-13	W1, W2, W3, W4		M1, AL1
Thu	4-Apr-13			
Fri	5-Apr-13	W1, W2, W3, W4	H1, H2, H3, H4	M2, M3, M4
Sat	6-Apr-13			
Sun	7-Apr-13			
Mon	8-Apr-13	W1, W2, W3, W4		M2, M3, M4
Tue	9-Apr-13			
Wed	10-Apr-13	W1, W2, W3, W4		M1, AL1
Thu	11-Apr-13			
Fri	12-Apr-13	W1, W2, W3, W4	H1, H2, H3, H4	
Sat	13-Apr-13			
Sun	14-Apr-13			
Mon	15-Apr-13	W1, W2, W3, W4		
Tue	16-Apr-13			
Wed	17-Apr-13	W1, W2, W3, W4		M1, AL1
Thu	18-Apr-13			
Fri	19-Apr-13	W1, W2, W3, W4	H1, H2, H3, H4	M2, M3, M4
Sat	20-Apr-13			
Sun	21-Apr-13			
Mon	22-Apr-13	W1, W2, W3, W4		
Tue	23-Apr-13			
Wed	24-Apr-13	W1, W2, W3, W4		M1, AL1,M2, M3, M4
Thu	25-Apr-13			
Fri	26-Apr-13	W1, W2, W3, W4	H1, H2, H3, H4	
Sat	27-Apr-13			
Sun	28-Apr-13			
Mon	29-Apr-13	W1, W2, W3, W4		
Tue	30-Apr-13			

Monitoring Day
Sunday or Public Holiday



Monitoring Schedule for next Reporting Period – May 2013

	N-4-	Stream Monitoring		NI-in- Manifester
Date		Water Sampling	Flow Monitoring	Noise Monitoring
Wed	1-May-13			
Thu	2-May-13			
Fri	3-May-13	W1, W2, W3, W4	H1, H2, H3, H4	
Sat	4-May-13			
Sun	5-May-13			
Mon	6-May-13	W1, W2, W3, W4		M1, AL1,M2, M3, M4
Tue	7-May-13			
Wed	8-May-13	W1, W2, W3, W4		
Thu	9-May-13			
Fri	10-May-13	W1, W2, W3, W4	H1, H2, H3, H4	
Sat	11-May-13			
Sun	12-May-13			
Mon	13-May-13	W1, W2, W3, W4	H1, H2, H3, H4	M1, AL1,M2, M3, M4
Tue	14-May-13			
Wed	15-May-13	W1, W2, W3, W4		
Thu	16-May-13			
Fri	17-May-13			
Sat	18-May-13	W1, W2, W3, W4	H1, H2, H3, H4	
Sun	19-May-13			
Mon	20-May-13	W1, W2, W3, W4		M1, AL1,M2, M3, M4
Tue	21-May-13			
Wed	22-May-13	W1, W2, W3, W4		
Thu	23-May-13			
Fri	24-May-13	W1, W2, W3, W4	H1, H2, H3, H4	
Sat	25-May-13			
Sun	26-May-13			
Mon	27-May-13	W1, W2, W3, W4		M1, AL1,M2, M3, M4
Tue	28-May-13			
Wed	29-May-13	W1, W2, W3, W4		
Thu	30-May-13			
Fri	31-May-13	W1, W2, W3, W4	H1, H2, H3, H4	

Monitoring Day
Sunday or Public Holiday



Appendix H

Meteorological Data of Reporting Period



Meteorological Data in Reporting Period

				Tai Po	Station	Shatin S	Station
Date		Weather	Total Rainfall (mm)	Mean Air Temp. (°C)	Mean Relative Humidity (%)	Wind Speed (km/h)	Wind Direction
1-Apr-13	Mon	Cloudy, showers, rain, winds from the north with rain.	0.1	20.6	81	10.4	E/SE
2-Apr-13	Tue	Cloudy, mist, rain, fresh, moderate easterly winds.	13.3	20.8	90.7	7.6	N/NE
3-Apr-13	Wed	Cloudy, showers, rain, winds from the north with rain.	9.2	18.9	88.5	12	E/NE
4-Apr-13	Thu	Cloudy, showers, rain, winds from the north with rain.	0.5	19.3	94	10.9	E/NE
5-Apr-13	Fri	Cloudy, showers, rain, squally thunderstorms, fresh southwesterly winds	34.7	23.1	91	13.7	S/SW
6-Apr-13	Sat	Cloudy, mist, rain, fresh, moderate easterly winds.	36.8	19.8	77		
7-Apr-13	Sun	Cloudy, rain, mist, moderate to fresh easterly winds.	0	16	60	6.2	E/NE
8-Apr-13	Mon	Cloudy, rain, mist, moderate to fresh easterly winds.	Trace	18.6	72.2	7	E/SE
9-Apr-13	Tue	Cloudy, rain, squally thunderstorms, moderate northeasterly winds, freshening later.	25.1	18.7	88.7	7.4	N/NE
10-Apr-13	Wed	Cloudy, rain, moderate northeasterly winds, fresh at times.	14.1	18.3	87.2	9.9	N/NE
11-Apr-13	Thu	Cloudy, rain, mist, moderate north to northeasterly winds.	13.8	17.3	84.5	8.1	N
12-Apr-13	Fri	Cloudy, rain, mist, moderate north to northeasterly winds.	2.1	17.2	84.7	7.1	N/NE
13-Apr-13	Sat	Cloudy, sunny intervals, light winds.	0	19	64	10	N/NE
14-Apr-13	Sun	Cloudy, sunny intervals, light winds.	0	22.6	65.5	7	W/SW
15-Apr-13		Sunny intervals, cloudy, mist, moderate easterly winds.	0	22.2	73	9.7	E/SE
16-Apr-13	Tue	Sunny intervals, cloudy, mist, moderate easterly winds.	0.4	22.6	88.5	6	N/NE
17-Apr-13	Wed	Cloudy, rain, mist, moderate north to northeasterly winds.	15.6	23.9	91.7	7.6	SW
18-Apr-13	Thu	Cloudy, showers, rain, squally thunderstorms, fresh southwesterly winds	8.2	25.7	82.5	10.7	SW
19-Apr-13	Fri	Cloudy, rain mist, moderate north to northeasterly winds.	8.9	24.7	91.5	10.2	S/SW
20-Apr-13	Sat	Cloudy, mist, rain, fresh, moderate easterly winds.	12.2	23.7	92	10	E/NE
21-Apr-13	Sun	Cloudy, sunny intervals, light winds.	0.3	21.5	88.5	12.4	E/NE
22-Apr-13		Cloudy, sunny intervals, light winds.	1	19.5	87	10.5	Е
23-Apr-13	Tue	Sunny intervals, cloudy, mist, moderate easterly winds.	0.5	22.5	84.2	8.5	E/SE
24-Apr-13	Wed	Cloudy, fog, squally thunderstorms, light winds.	0	25.3	81	9.1	S/SW
25-Apr-13	Thu	Warm, sunny, moist.	30.3	27	78.7	10.5	S/SW
26-Apr-13	Fri	Cloudy, rain, moderate to fresh easterly winds	2.9	22	75.5	10.5	E
27-Apr-13	Sat	Warm, sunny, moist.	Trace	1.6	89	14	E/SE
28-Apr-13		Cloudy, rain, moderate to fresh easterly winds	Trace	21.7	90.5	9.9	E/NE
29-Apr-13		Cloudy, fog, squally thunderstorms, light winds.	Trace	23.6	91	11.4	E/SE
30-Apr-13	Tue	Cloudy, fog, squally thunderstorms, light winds.	23.8	25.8	82.2	16.2	SW

^{*} The record was downloaded from The Hong Kong Observatory Weather Stations



Appendix I

Data Base of Monitoring Results



Construction Noise Measurement Data

Designated Monitoring Station – M1 (14, Shuen Wan Chim Uk)

Date	Start Time	1 st Leq _{5min}	2 nd Leq _{5min}	3 rd Leq _{5min}	4 th Leq _{5min}	5 th Leq _{5min}	6 th Leq _{5min}	$ m Leq_{30min^*}$
3-Apr-13	10:15	-	ı	-	-	-	-	64.3
10-Apr-13	13:50	-	ı	-	-	-	ı	63.6
17-Apr-13	9:00	-	ı	-	-	-	ı	66.9
24-Apr-13	12:40	-	ı	-	-	-	ı	61.8
Limit I	Level				-			> 75 dB(A)

^(*)The monitoring is undertaken under façade situation. No façade correction is added according to acoustical principles and EPD guidelines.

Designated Monitoring Station - AL1 (Joint Village Office for Villages in Shuen Wan, Tai Po)

Date	Start Time	1st Leq5m in	2nd Leq5m in	3rd Leq5m in	4th Leq5m in	5th Leq5m in	6th Leq5m in	Leq30min*
3-Apr-13	10:50	-	-	-	-	-	-	66.1
10-Apr-13	14:25	-	-	-	-	-	-	63.5
17-Apr-13	9:40	-	-	-	-	-	-	68.3
24-Apr-13	13:15	-	-	-	-	-	_	62.1
Limit 1	Level			ı	•			> 75 dB(A)

^(*)The monitoring is undertaken under façade situation. No façade correction is added according to acoustical principles and EPD guidelines.

Designated Monitoring Station - M2 (150, San Tau Kok)

Date	Start Time	1 st Leq _{5min}	2 nd Leq _{5min}	3 rd Leq _{5min}	4 th Leq _{5min}	5 th Leq _{5min}	6 th Leq _{5min}	Leq _{30min}	Corrected* Leq _{30min}
5-Apr-13	16:00	60.9	61.5	63.1	51.7	60.1	61.5	60.8	63.8
8-Apr-13	9:40	70.3	67.7	70.0	66.8	67.9	66.1	68.4	71.4
19-Apr-13	9:23	66.2	74.3	73.6	72.2	71.7	67.4	71.8	74.8
24-Apr-13	13:00	65.5	65.7	64.2	63.0	63.9	64.4	64.5	67.5
Limit Level					-			> 75	dB(A)

^(*) A façade correction of +3 dB(A) has been added according to acoustical principles and EPD guidelines.

Designated Monitoring Station – M3 (31, Wai Ha)

Date	Start Time	1 st Leq _{5min}	2 nd Leq _{5min}	3 rd Leq _{5min}	4 th Leq _{5min}	5 th Leq _{5min}	6 th Leq _{5min}	Leq _{30min}	Corrected* Leq _{30min}
5-Apr-13	15:24	60.8	60.8	63.8	58.9	63.0	60.4	61.6	64.6
8-Apr-13	10:25	65.4	67.0	59.6	63.1	65.6	62.3	64.5	67.5
19-Apr-13	10:00	64.0	65.5	62.1	59.2	59.7	62.3	62.7	65.7
24-Apr-13	13:40	61.7	61.2	63.8	62.0	61.6	61.7	62.1	65.1
Limit 1	Level				•			> 75	5 dB(A)

^(*) A façade correction of +3 dB(A) has been added according to acoustical principles and EPD guidelines.

Designated Monitoring Station – M4 (Block 15, Treasure Spot Garden)

Date	Start Time	1 st Leq _{5min}	2 nd Leq _{5min}	3 rd Leq _{5min}	4 th Leq _{5min}	5 th Leq _{5min}	6 th Leq _{5min}	Leq _{30min}	Corrected* Leq _{30min}
5-Apr-13	15:30	54.3	55.8	53.6	54.1	54.8	53.2	54.4	57.4
8-Apr-13	11:18	54.1	53.2	56.5	54.9	54.0	55.7	54.9	57.9
19-Apr-13	10:45	49.6	48.5	50.0	49.8	49.2	50.3	49.6	52.6
24-Apr-13	14:15	59.5	58.6	59.7	60.9	60.8	58.9	59.8	62.8
Limit 1	Level			i	•			> 75	5 dB(A)

 $^{(*)\} A\ façade\ correction\ of\ +3\ dB(A)\ has\ been\ added\ according\ to\ acoustical\ principles\ and\ EPD\ guidelines.$

AUES

Location					DO (r	ng/L)	DO	(%)	Turbidit	y (NTU)	р	Н	SS(m	g/L)
M1 (impact)					Action	7.27	Action	n/a	Action	4.77	Action	n/a	Action	9.73
W1 (impact)					Limit	4	Limit	n/a	Limit	5.26	Limit	n/a	Limit	10.77
W2 (impact)					Action	7.26	Action	n/a	Action	2.46	Action	n/a	Action	8.89
wz (iiiipact)		Action/ Limi	t Level		Limit	4	Limit	n/a	Limit	3.42	Limit	n/a	Limit	9.75
W3 (control)					n	/a	n,	′a	n,	/a	n	/a	n/	'a
W4 (impact)						9.27	Action	n/a	Action	3.32	Action	n/a	Action	6.98
vv+ (impact)						4	Limit	n/a	Limit	4.52	Limit	n/a	Limit	7.66
Date	3-Apr-13													
Location	Time	Depth (m)	Temp	(oC)	n) OD	ng/L)	DO	(%)	Turbidit	y (NTU)	р	Н	SS(m	g/L)
W1 - ebb (impact)	17:00	0.30	24.2	23.6	7.15 7.01	7.1	84.9 83.2	84.1	6.4	6.4	8.55 8.57	8.6	9	9.0
W1- flood (impact)	11:00	0.30	24.1 22.6	23.4	7.01 6.84	6.9	82.7 80.7	81.7	6.6 5.1	5.9	8.69 8.67	8.7	10 10	10.0
W2 (Impact)	10:15	<1	19.8 19.8	19.8	7.18 7.18	7.2	84 84	84.0	2.1 2.1	2.1	7.96 7.96	8.0	1.2 1.2	1.2
W3 (control)	11:30	0.20	24.2 23	23.6	6.91 6.83	6.9	82.2 81	81.6	4.5 3.8	4.2	8.35 8.34	8.3	26 26	26.0
W4 (impact)	11:40	0.15	24 23.4	23.7	6.39 6.31	6.4	76.4 75.6	76.0	7.1 7.5	7.3	8.55 8.54	8.5	84 84	84.0

Date	5-Apr-13													
Location	Time	Depth (m)	Temp	(oC)	1) OQ	ng/L)	DO	(%)	Turbidit	y (NTU)	p	Н	SS(m	ig/L)
W1 - ebb (impact)	9:00	0.30	22.6 22.2	22.4	6.82 6.71	6.8	79.8 78.7	79.3	4.3 4.5	4.4	8.83 8.84	8.8	26 26	26.0
W1- flood (impact)	13:00	0.30	22.6 22.2	22.4	7.6 7.51	7.6	89 87.9	88.5	5.6 5.3	5.5	8.92 8.91	8.9	33 33	33.0
W2 (Impact)	10:40	<1	21.3 21.3	21.3	7.88 7.88	7.9	95 95	95.0	2.8	2.8	7.56 7.56	7.6	2	2.0
W3 (control)	9:25	0.20	22.7 22.2	22.5	7.45 7.28	7.4	87.1 85	86.1	7 6.68	6.8	8.24 8.23	8.2	4	4.0
W4 (impact)	9:15	0.15	22.7 22.2	22.5	7.47 7.35	7.4	87.3 86	86.7	8.2 7.9	8.1	8.4 8.39	8.4	15 15	15.0

Date	8-Apr-13													
Location	Time	Depth (m)	Temp	(oC)	DO (r	mg/L)	DO	(%)	Turbidit	y (NTU)	р	Н	SS(m	g/L)
W1 - ebb (impact)	11:18	0.80	22.7 22.8	22.8	6.82 6.85	6.8	74.9 74.2	74.6	9.98 10.1	10.0	7.68 7.79	7.7	34 34	34.0
W1- flood (impact)	17:07	1.20	21.6	21.6	6.14	6.1	68.8	68.4	7.04	7.0	8.25 8.13	8.2	10 10	10.0
W2 (Impact)	12:30	<1	19.5 19.5	19.5	7.89 7.89	7.9	88 88	88.0	3.2	3.2	7.46 7.46	7.5	1	1.0
W3 (control)	11:08	0.30	21.4 21.5	21.5	6.7 6.64	6.7	75.1 74.7	74.9	12.8 12.4	12.6	8.42 8.56	8.5	80 80	80.0
W4 (impact)	11:00	0.20	21.2	21.3	7.57 7.38	7.5	84.2 83	83.6	3.81 4.49	4.2	8.78 8.7	8.7	7	7.0

Date	10-Apr-13													
Location	Time	Depth (m)	Temp	(oC)	1) OD	ng/L)	DO	(%)	Turbidit	y (NTU)	p	Н	SS(m	ıg/L)
W1 - ebb	12:30	0.70	23.9	23.9	5.38	5.3	63.2	63.0	18.7	19.1	7.76	7.7	11	11.0
(impact)	12.50	0.70	23.8	25.7	5.31	3.3	62.7	05.0	19.5	17.1	7.73	7.7	11	11.0
W1- flood	17:00	1.00	24	23.9	5.28	5.2	62.3	62.0	20.8	20.7	7.31	7.4	11	11.0
(impact)	17.00	1.00	23.8	23.9	5.19	5.2	61.7	02.0	20.5	20.7	7.4	7.4	11	11.0
W2 (Impact)	13:50	<1	21.3	21.3	7.48	7.5	85	85.0	7.9	7.9	7.48	7.5	15	15.0
wz (iiipaci)	13.30	< 1	21.3	21.3	7.48	7.5	85	65.0	7.9	7.9	7.48	7.5	15	15.0
W3 (control)	16:30	0.35	23.4	23.4	5.53	5.4	65	63.4	1.88	1.9	8.35	8.3	<2	2.0
W3 (COITHOI)	10.30	0.33	23.3	23.4	5.25	5.4	61.8	03.4	1.87	1.9	8.27	0.3	<2	2.0
W4 (impact)	10:00	0.20	25	25.0	5.33	5.3	64.6	64.2	21.9	22.2	7.94	7.9	14	14.0
vv4 (impact)	10:00	0.20	24.9	25.0	5.27	5.3	63.7	04.2	22.5	22.2	7.89	7.9	14	14.0

Date	12-Apr-13													
Location	Time	Depth (m)	Temp	(oC)	1) OD	ng/L)	DO	(%)	Turbidit	y (NTU)	p	Н	SS(m	g/L)
W1 - ebb (impact)	13:00	0.60	21.7 21.5	21.6	5.81 5.78	5.8	66 65.5	65.8	4.49 4.19	4.3	7.82 8	7.9	<u>5</u>	5.0
W1- flood (impact)	9:00	1.10	22.9 22.7	22.8	5.93 5.9	5.9	69 68.5	68.8	4.7 4.44	4.6	7.85 7.88	7.9	5 5	5.0
W2 (Impact)	15:10	<1	21.8 21.8	21.8	8.06 8.06	8.1	100 100	100.0	3.3	3.3	7.66 7.66	7.7	4.8 4.8	4.8
W3 (control)	13:30	0.35	21.4 21.5	21.5	6.55 6.51	6.5	74.3 73.8	74.1	6.84 5.3	6.1	8.36 8.31	8.3	10 10	10.0
W4 (impact)	13:20	0.20	21.1 21.3	21.2	6.31	6.3	71.1 71.2	71.2	6.91 7.44	7.2	7.92 7.91	7.9	8	8.0

Date	15-Apr-13													
Location	Time	Depth (m)	Temp	(oC)	1) OQ	ng/L)	DO	(%)	Turbidity (NTU)		рН		SS(mg/L)	
W1 - ebb	15:00	1.00	24.9	25.1	5.56	5.6	68	68.2	2.03	1.9	8.34	8.3	6	6.0
(impact)	15.00	1.00	25.3	25.1	5.59	3.0	68.4	00.2	1.86	1.7	8.33	0.5	6	0.0
W1- flood	9:00	1.20	24.8	24.9	5.4	5.4	65.9	66.0	1.9	1.8	8.68	8.7	7	7.0
(impact)	7.00	1.20	25	24.7	5.39	5.4	66.1	00.0	1.77	1.0	8.65	0.7	7	7.0
W2 (Impact)	15:10	<1	23.1	23.1	7.13	7.1	80	80.0	2.5	2.5	7.36	7.4	8.4	8.4
wz (iiipaci)	13.10	<u> </u>	23.1	23.1	7.13	7.1	80	00.0	2.5	2.5	7.36	7.4	8.4	0.4
W3 (control)	15:30	0.20	24.8	24.7	5.46	5.5	66.5	66.5	2.23	2.1	8.11	8.1	3	3.0
W3 (COITHOI)	15.50	0.20	24.6	24.7	5.45	5.5	66.4	00.5	1.95	2.1	8.06	0.1	3	3.0
W4 (impact)	15:20	0.15	24.4	24.5	5.27	5.3	64	63.9	50.7	48.3	8.27	8.3	30	30.0
W4 (IIIIpact)	15.20	0.15	24.6	24.3	5.25	5.5	63.8	03.9	45.8	40.3	8.33	0.3	30	30.0

Date	17-Apr-13													
Location	Time	Depth (m)	Temp	Temp (oC)		DO (mg/L)		DO (%)		Turbidity (NTU)		Н	SS(mg/L)	
W1 - ebb	16:00	0.30	23.7	23.9	5.5	5.4	66.5	65.4	5.77	5.7	7.3	7.3	11	11.0
(impact)	10.00	0.30	24.1	23.9	5.31	3.4	64.2	03.4	5.71	5.7	7.33	7.3	11	11.0
W1- flood	9:30	0.30	23.9	24.2	4.94	4.9	59.6	59.1	6.02	6.0	7.67	7.7	12	12.0
(impact)	9.30	0.30	24.5	24.2	4.85	4.9	58.6	39.1	5.89	0.0	7.69	7.7	12	12.0
W2 (Impact)	16:00	<1	21.1	21.1	6.86	6.9	70	70.0	5.6	5.6	8.1	8.1	3.4	3.4
vvz (mipact)	10.00	< I	21.1	21.1	6.86	0.9	70	70.0	5.6	5.0	8.1	0.1	3.4	3.4

DSD Contract No. DC/2010/02 Contract No. - Drainage Improvement in Shuen Wan and Shek Wu Wai Summary of Water Quality Monitoring Results

AUES

Location					DO (r	ng/L)	DO (%)		Turbidity (NTU)		pН		SS(mg/L)	
W1 (impact)					Action	7.27	Action	n/a	Action	4.77	Action	n/a	Action	9.73
wir (iiripact)					Limit	4	Limit	n/a	Limit	5.26	Limit	n/a	Limit	10.77
W2 (impact)					Action	7.26	Action	n/a	Action	2.46	Action	n/a	Action	8.89
wz (impact)	, i	Action/ Limi	it Level		Limit	4	Limit	n/a	Limit	3.42	Limit	n/a	Limit	9.75
W3 (control)					n	n/a		n/a		/a	n	/a	n/	'a
W4 (impact)					Action	9.27	Action	n/a	Action	3.32	Action	n/a	Action	6.98
(Limit	4	Limit	n/a	Limit	4.52	Limit	n/a	Limit	7.66
W3 (control)	9:00	0.25	23.9	24.1	6.1	6.0	73.7	72.7	4.48	4.3	7.37	7.4	4	4.0
ws (control)	7.00	0.23	24.2	24.1	5.93	0.0	71.6	12.1	4.11	4.5	7.36	7.4	4	4.0
W4 (impact)	9:05	0.15	23.8	24.1	7.04	7.0	85.2	84.2	8.41	8.3	7.6	7.6	4	4.0
www (iiiipact)	7.00	0.15	24.3	24.1	6.88	7.0	83.2	04.2	8.1	0.3	7.64	7.0	4	4.0

Date	19-Apr-13													
Location	Time	Depth (m)	Temp	(oC)	DO (r	ng/L)	DO	(%)	Turbidity (NTU)		рН		SS(m	g/L)
W1 - ebb (impact)	17:30	0.80	24.7 26.4	25.6	6.13	6.1	74.5 74	74.3	20.8 19.7	20.3	8.03	8.0	17 17	17.0
W1- flood (impact)	9:00	1.10	26 24.9	25.5	5.67 5.61	5.6	69 68.5	68.8	21.7 18.2	20.0	7.76 7.83	7.8	16 16	16.0
W2 (Impact)	15:50	<1	22.3 22.3	22.3	6.89 6.89	6.9	75 75	75.0	2	2.0	7.35 7.35	7.4	2.6 2.6	2.6
W3 (control)	17:00	0.25	24.8 26	25.4	5.79 5.65	5.7	70.2 68.9	69.6	7.34 5.81	6.6	7.99 7.88	7.9	13 13	13.0
W4 (impact)	17:15	0.15	24.9 26.7	25.8	5.62 5.56	5.6	68.8 68.2	68.5	16.7 17	16.9	8.1 8.07	8.1	14 14	14.0

Date	22-Apr-13													
Location	Time	Depth (m)	Temp	(oC)	1) OD	ng/L)	DO	(%)	Turbidity (NTU)		p	Н	SS(m	ıg/L)
W1 - ebb (impact)	10:00	0.35	23.9 23	23.5	4.89 4.8	4.8	58.4 58.2	58.3	6.76 5.69	6.2	7.7 7.68	7.7	8	8.0
W1- flood (impact)	16:00	0.35	23 23.8	23.4	4.64 4.62	4.6	55.3 55.1	55.2	5.52 6.11	5.8	7.7 7.72	7.7	9	9.0
W2 (Impact)	11:10	<1	21.3 21.3	21.3	6.79 6.79	6.8	70 70	70.0	2.9	2.9	7.89 7.89	7.9	6.2	6.2
W3 (control)	10:15	0.25	23.3 23.9	23.6	5.62 5.6	5.6	67.1 67	67.1	4.68 3.99	4.3	7.91 7.87	7.9	2	2.0
W4 (impact)	10:30	0.10	23.4 23.9	23.7	5.29 5.27	5.3	62.9 62.3	62.6	30 29.6	29.8	8.25 8.23	8.2	16 16	16.0

Date	24-Apr-13													
Location	Time	Depth (m)	Temp	(oC)	1) OQ	ng/L)	DO	(%)	Turbidit	y (NTU)	p	Н	SS(m	ıg/L)
W1 - ebb	11:10	0.50	25.1	25.1	8.44	8.3	109.7	104.3	6.94	7.0	7.97	8.0	25	25.0
(impact)	11.10	0.50	25	25.1	8.09	0.5	98.9	104.5	7.03	7.0	8.04	0.0	25	23.0
W1- flood	17:30	0.40	25.1	26.4	6.84	6.8	83.9	83.5	1.57	1.5	8.86	8.8	<2	2.0
(impact)	17.30	0.40	27.6	20.4	6.78	0.0	83.1	63.5	1.45	1.5	8.82	0.0	<2	2.0
W2 (Impact)	12:40	<1	23.1	23.1	7.34	7.3	85	85.0	6.9	6.9	7.88	7.9	13	13.0
wz (IIIIpaci)	12.40	< 1	23.1	23.1	7.34	7.3	85	65.0	6.9	0.9	7.88	7.9	13	13.0
W3 (control)	10:50	0.20	25	26.5	7.44	7.3	90.5	89.4	13.3	12.8	8.06	8.1	51	51.0
ws (control)	10:50	0.20	28	20.5	7.23	7.3	88.3	89.4	12.3	12.8	8.07	8.1	51	51.0
MA (impost)	10:40	0.10	25	26.3	7.01	7.0	85.9	85.2	7.2	7.8	8.7	8.7	32	32.0
W4 (impact)	10:40	0.10	27.6	20.3	6.9	7.0	84.5	85.2	8.3	7.8	8.66	8.7	32	32.0

Date	26-Apr-13							•	•		•	•		
Location	Time	Depth (m)	Temp	(oC)	DO (r	ng/L)	DO	(%)	Turbidity (NTU)		pН		SS(mg/L)	
W1 - ebb (impact)	12:00	0.30	25.2 25.5	25.4	4.84 4.73	4.8	59.1 57.7	58.4	11.1 10.6	10.9	7.47 7.51	7.5	51 51	51.0
W1- flood (impact)	17:00	0.40	24.7 23.2	24.0	5.69 5.65	5.7	68.9 68.5	68.7	9.25 8.61	8.9	7.64 7.62	7.6	9	9.0
W2 (Impact)	14:00	<1	21.9 21.9	21.9	7.78 7.78	7.8	85 85	85.0	2	2.0	7.88 7.88	7.9	4.8 4.8	4.8
W3 (control)	12:30	0.15	24.5 23.4	24.0	5.55 5.5	5.5	66.9 66.5	66.7	12.8 13.1	13.0	7.35 7.4	7.4	29 29	29.0
W4 (impact)	12:15	0.10	23.2 24.5	23.9	5.5 5.48	5.5	66.3 66.1	66.2	47.9 49.3	48.6	7.66 7.63	7.6	59 59	59.0

Date	29-Apr-13													
Location	Time	Depth (m)	Temp	(oC)	n) OD	mg/L)	DO	(%)	Turbidity (NTU)		pН		SS(m	ıg/L)
W1 - ebb (impact)	14:00	0.30	25.1 23.9	24.5	6.27 6.01	6.1	76.7 74.1	75.4	4.3 4.35	4.3	8.15 8.16	8.2	13 13	13.0
W1- flood (impact)	9:00	0.35	25.2 23.7	24.5	5.24 5.18	5.2	64.1 63.1	63.6	0.82	0.9	8.82 8.83	8.8	24 24	24.0
W2 (Impact)	16:10	<1	22.3 22.3	22.3	7.71 7.71	7.7	85 85	85.0	3	3.0	8.79 8.74	8.8	5.6 5.6	5.6
W3 (control)	9:15	0.15	25.6 25.7	25.7	4.77 4.72	4.7	58.9 58.3	58.6	0.43	0.3	8.5 8.56	8.5	2	2.0
W4 (impact)	9:20	0.10	26.5 24.5	25.5	5.77 5.7	5.7	72.4 71.4	71.9	5.04 4.59	4.8	8.69 8.68	8.7	6	6.0




Appendix J


Graphical Plots of Impact Monitoring – Noise, Water Quality and Hydrological Characteristics




Graphic Plot – Construction Noise



Remark: The monitoring is undertaken under façade situation. No façade correction is added according to acoustical principles and EPD guidelines.




Remark: The monitoring is undertaken under façade situation. No façade correction is added according to acoustical principles and EPD guidelines.

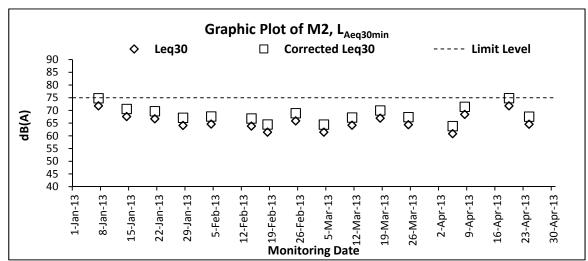


Remark: The monitoring is undertaken under free field situation. A façade correction of +3 dB(A) has been added according to acoustical principles and EPD guidelines.



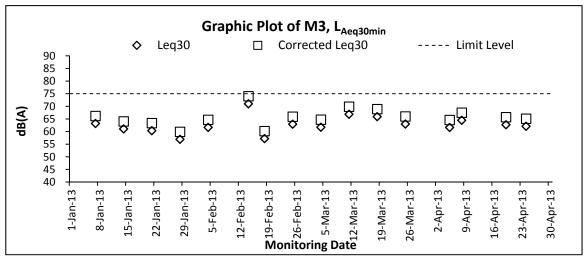


Remark: The monitoring is undertaken under free field situation. A façade correction of +3 dB(A) has been added according to acoustical principles and EPD guidelines

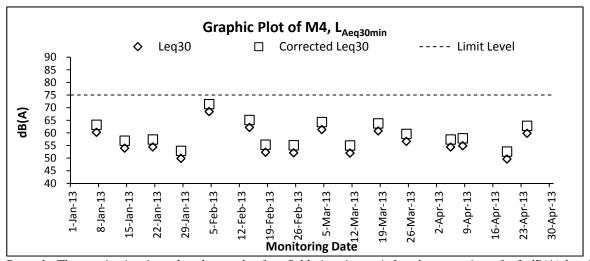



Remark: The monitoring is undertaken under free field situation. A façade correction of +3 dB(A) has been added according to acoustical principles and EPD guidelines




Graphic Plot – Water Quality

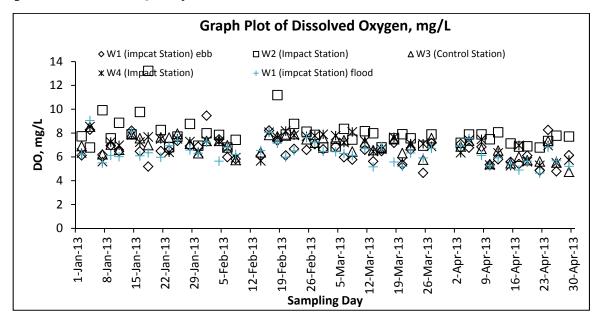

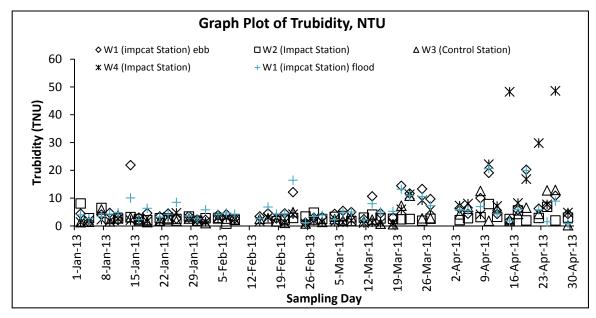

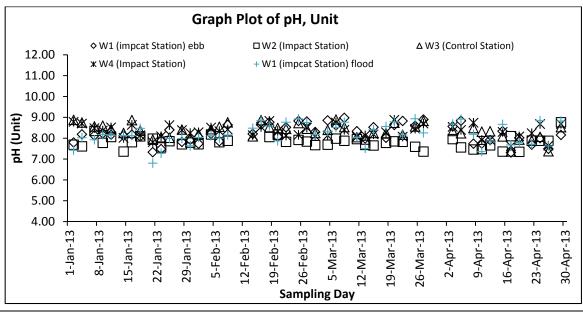





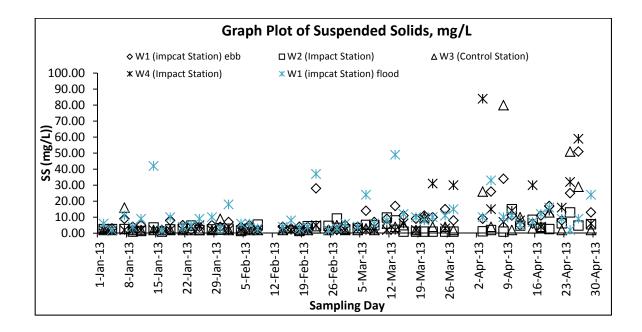




Graphic Plot – Hydrological Characteristics (Water Depth)

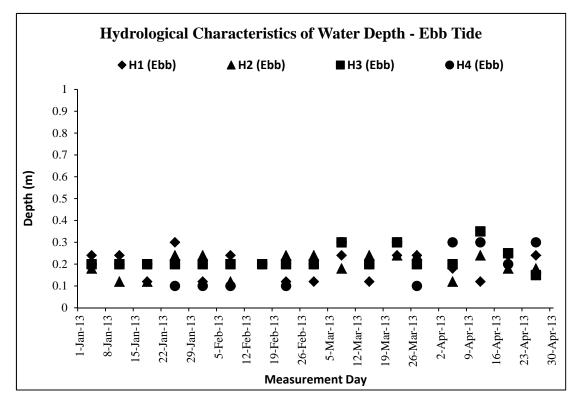


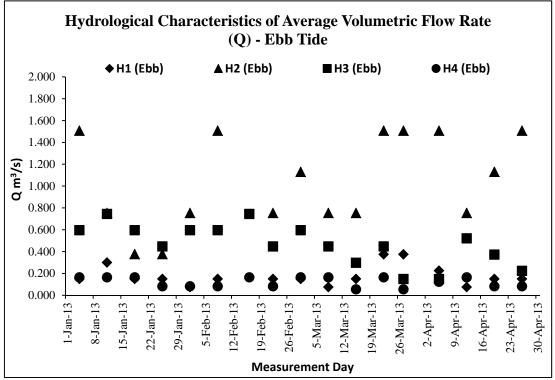



Graphic Plot – Hydrological Characteristics (Water Flow Rate)

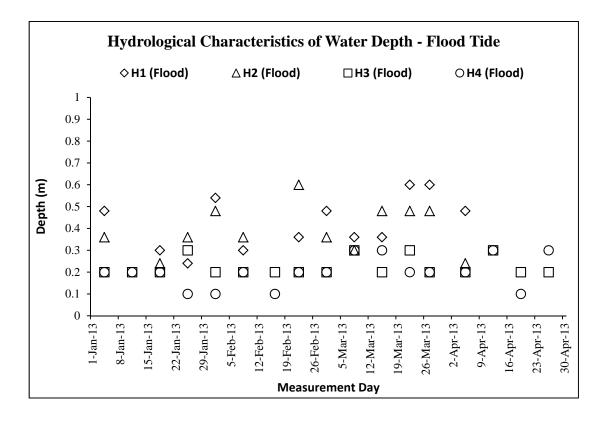

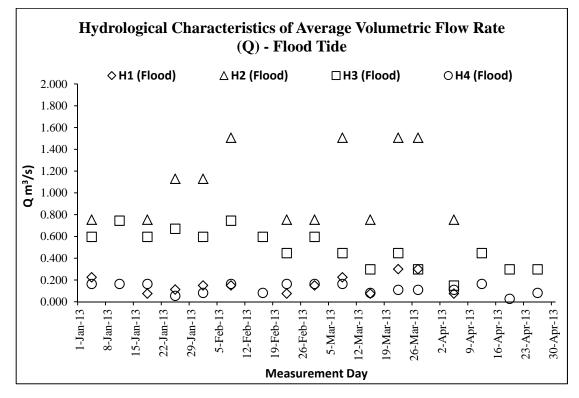



Appendix K

Monthly Summary Waste Flow Table

Monthly Summary Waste Flow Table for <u>2011 to 2013</u> (Year)

Name of Department: DSD

			ivionting	Summary v	v aste 1 10 v	Tuble loi	2011 to 2013 (1eal)					
	Actual Quantities of Inert C&D Materials Generated Monthly						Actu	Actual Quantities of C&D Wastes Generated Monthly				
onth	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse	
	(in '000m ³)	(in '000m ³)	$(in '000m^3)$	(in '000m ³)	$(in '000m^3)$	$(in '000m^3)$	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)	
Apr 2011	Nil	0	0	0	0	0	0	0	0	0	0	
May 2011	Nil	0	0	0	0	0	0	0	0	0	0	
June 2011	Nil	0	0	0	0	0	0	0	0	0	0	
July 2011	Nil	0	0	0	0	0	0	0	0	0	0	
Aug 2011	0.7855	0	0	0.7855	0	0	0	0	0	0	0	
Sept 2011	Nil	0	0	0	0	0	0	0	0	0	0	
Oct 2011	Nil	0	0	0	0	0	0	0	0	0	0.02	
Nov 2011	Nil	0	0	0	0	0	0	0	0	0	0.045	
Dec 2011	0.08	0	0	0	0.08	0	0	0	0	0	0	
Jan 2012	Nil	0	0	0	0	0	0	0	0	0	0.01	
Feb 2012	0.01	0	0	0	0.01	0	0	0	0	0	0.03	
Mar 2012	0.405	0	0	0	0.405	0	0	0	0	0	0	
Apr 2012	0.005	0	0	0	0.005	0	0	0	0	0	0	
May 2012	0.165	0	0	0	0.165	0	0	0	0	0	0	
June 2012	0.145	0	0	0	0.145	0	0	0	0	0	0.035	
July 2012	0.005	0	0	0	0.005	0	0	0	0	0	0.005	
Aug 2012	0.775	0	0	0	0.775	0	0	0	0	0	0	
Sept 2012	0.21	0	0	0	0.21	0	0	0	0	0	0	
Oct 2012	0.49	0	0	0	0.49	0	0	0	0	0	0	
Nov 2012	0	0	0	0	0	0	0	0	0	0	0.03	
Dec 2012	0	0	0	0	0	0	0	0	0	0	0.01	
Jan 2013	0.035	0	0	0	0.035	0	0	0	0	0	0.025	
Feb. 2013	0.035	0	0	0	0.035	0	0	0	0	0	0.005	
Mar. 2013	0.002	0	0	0	0.002	0	0	0	0	0	0.005	
Apr. 2013	0.31	0	0	0	0.31	0	0	0	0	0	0.005	
Total	3.4575	0	0	0.7855	2.672	0	0	0	0	0	0.225	

	Forecast of Total Quantities of C&D Materials to be Generated from the Contract*									
Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
$(in '000m^3)$	(in '000m ³)	$(in '000m^3)$	$(in '000m^3)$	$(in '000m^3)$	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
23	1	10	0	10	2	5	2	1	1	3

Name of Department: DSD

Notes:

- (1) The performance targets are given in ETWB Technical Circular PS Clause 6(14).
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material
- The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m3. (ETWB Technical Circular PS Clause 5(4)(b) refers). [Delete Note (4) and the table above on the forecast, where inapplicable].

Summary Table for Work Processes or Activities Requiring Timber for Temporary Works

Name of Department: DSD

Contract No. : <u>DC/2010/02</u>

Contract Title: Drainage Improvement Works in Shuen Wan and Shek Wu Wai

Item No.	Description of Works Process or Activity [see note (a) below]	Justifications for Using Timber in Temporary Construction Works	Est. Quantities of Timber Used (m3)	Actual Quantities used (m3)	Remarks
1.	Formwork for concreting	Easy handle by manpower	0.71	0.7	
2.					
3.					
4.					
5.					
6.					
7.				_	
8.					
		Total Estimated Quantity of Timber Used	0.71		

Notes:

- a. The Contractor shall list out all the work items requiring timber for use in temporary construction works. Several minor work items may be grouped into one for ease of updating.
- b. The summary table shall be submitted to the *Architect/Engineer's Representative monthly together with the Waste Flow Table for review and monitoring in accordance with the ETWB Technical Circular 19/2005 PS sub-clause 5(5) in Appendix C.



Appendix L

Monthly Landscape & Visual Inspection Report

Contract No. DC/2010/02 Drainage Improvement Works in Shuen Wan and Shek Wu Wai Bi-weekly Landscape & Visual Monitoring

EM&A (Landscape & Visual) Report (April 2013) (Issue 1)

Job Ref.: 09/317/161D KLKJV-SW

Date: May 2013



Contract No. DC/2010/02 Drainage Improvement Works in Shuen Wan and Shek Wu Wai Bi-weekly Landscape & Visual Monitoring

EM&A (Landscape & Visual) Report (April 2013)

(Issue 1)

May 2013

	Name	Signature
Prepared by:	Sean FONG	A)
Reviewed by:	lda YU	Elayn
Date:	6 th May 2013	U

Job Ref.: 09/317/161D KLKJV-SW

CONTENTS

1	INTRODUCTION	1
2	SCOPE OF MONITORING	1
- 3	LANDSCAPE & VISUAL MONITORING RESULTS	2
	AUDIT SCHEDULE	

LIST OF APPENDICES

Appendix A – Photographs



Contract No. DC/2010/02 Drainage Improvement Works in Shuen Wan and Shek Wu Wai

Bi-weekly Landscape & Visual Monitoring Job Ref.: 09/317/161D KLKJV -SW

EM&A (Landscape & Visual) Report (April 2013) (Issue 1)

1 INTRODUCTION

- 1.1.1 The Landscape and Visual Monitoring of the Project is conducted to fulfill Clauses 5.2 and 5.4 of EP-303/2008 and the monitoring requirements in accordance with Section 7 of the approved updated EM&A Manual (approved by EPD on 31st May 2012) of the Project. A Baseline Review on updating the landscape and visual condition, and the mitigation measures of the Project (including Contracts 1 and 2 of the Project) was undertaken before the commencement of the Project. The review findings were updated in the Baseline Environmental Monitoring Report submitted to the EPD on 14th February 2011.
- 1.1.2 This monthly monitoring report will detail the scope of landscape and visual monitoring work, monitoring findings and observations, and any recommendation and advice on proper implementation of the landscape mitigation measures in the works areas under Contract 2 of the Project.

2 SCOPE OF MONITORING

2.1 Monitoring objectives

2.1.1 Landscape and Visual Monitoring of the Project should be conducted on a bi-weekly basis for checking the design, implementation and maintenance of the landscape and visual mitigation measures throughout the construction phase and in a quarterly basis during operational phase of the Project. Observations of any potential conflicts between the proposed mitigation measures and the project works carried out by the Contractors should be recorded. Recommendation and advice on proper implementation of the landscape mitigation measures should be provided to the Contractor for minimizing any potential impacts on the landscape and visual elements.

2.2 Monitoring during Construction Phase

- 2.2.1 The following landscape and visual mitigation measures should be implemented during the construction phase of the project to minimize the potential impacts:
 - Visual Screen Use of hoardings as visual screens for the construction in the works areas;
 - Contaminant/ Sediment Control Use of temporary barriers, covers and drainage provision around the construction works as contaminant/ sediment control to prevent the contaminants and sediments from entering the sensitive water-based habitats;
 - Pollution Control Implementation of pollution control measures to minimize any adverse environmental impacts to the surrounding habitats;
 - Liaison with Nursery (Not relevant to Contract 2 of the Project) Liaison with the
 nursery operator as necessary to minimize any adverse impact to the daily operation
 and plant holding capacity of the nursery;
 - Existing Trees within Works Area Maintenance and protection of the existing trees, especially their crowns, trunks and roots, within work sites; and
 - Construction Light Provision of construction light should be controlled at night to avoid excessive glare to the surrounding villages and to Plover Cove.



Drainage Improvement Works in Shuen Wan and Shek Wu Wai

Bi-weekly Landscape & Visual Monitoring

Job Ref.: 09/317/161D KLKJV -SW

EM&A (Landscape & Visual) Report (April 2013) (Issue 1)

2.3 Monitoring during Operational Phase

- 2.3.1 The following landscape and visual mitigation measures should be implemented during the operational phase of the project to minimize the potential impacts:
 - Viewing area formation by planting with shrubs, grasses and benches along the area;
 - Architectural design of the pump house will help it fit into the existing suburban, natural
 to semi-natural surroundings (Not relevant to Contract 2 of the Project);
 - Landscape design of pump house by providing sufficient planting around its boundary fence (Not relevant to Contract 2 of the Project);
 - Enhancement planting along Tung Tsz Road with shrubs/ trees of suitable species to help protect the stream and marshes;
 - Construction of box culvert should be with at least 1.0m soil depth for enhancement planting;
 - Transplanting of existing affected trees to adjacent locations should be carried out;
 - Preparation for transplanting is needed to allow sufficient time for root pruning and rootball preparation prior to transplanting; and
 - Reinstatement of affected area should be carried out to check that the works areas are properly reinstated.

3 LANDSCAPE & VISUAL MONITORING RESULTS

3.1 Monitoring Date(s)

- 3.1.1 This monthly Landscape and Visual Monitoring (April 2013) was conducted to cover only areas of Contract 2 of the Project (i.e. the construction of a twin-cell box culvert close to Shuen Wan Conservation Area and Wai Ha River along Tung Tsz Road, and a drainage pipe near Wai Ha Village). The bi-weekly monitoring was conducted on 5th, 18th and 30th April 2013.
- 3.1.2 All photos stated in this section are recorded in **Appendix A**.

3.2 Visual Screen

3.2.1 No follow-up action by the Contractor is required as from the *Monthly EM&A Report for March 2013*.

Observation

- 3.2.2 Temporary hoardings, in the form of construction barriers, have been erected from west to east parts along Tung Tsz Road from the opposite side of Wai Ha to the opposite side of San Tau Kwok. The construction works along the access road from Tung Tsz Road towards Treasure Spot Garden II has been also demarcated with temporary construction barriers. Another section of temporary hoardings has been erected next to the path outside Treasure Spot Garden II. **Photos 1-4** show the views of the erected hoardings along the active works area under Contract 2.
- 3.2.3 No hoardings have been erected along the rest of the proposed works area since neither construction works nor any associated preparation works have been commenced.



Drainage Improvement Works in Shuen Wan and Shek Wu Wai

Bi-weekly Landscape & Visual Monitoring

Job Ref.: 09/317/161D KLKJV -SW

EM&A (Landscape & Visual) Report (April 2013) (Issue 1)

- To the southeast of Jade View Villa and adjacent to the current active works area, a demarcated wetland rehabilitation area has been maintained by parties other than the Project Proponent, the Project's Contractor and Sub-contractors since January 2012. The wetland rehabilitation area has been surrounded by red strings since April 2012 (**Photo 5**). No vegetation clearance or any other works were observed within this wetland rehabilitation area. Large rocks and construction materials were dumped close to the wetland rehabilitation area as inspected on 30th April 2013 (**Photos 6-7**).
- 3.2.5 Dumping on the Taro field located along the path towards the Treasure Spot Garden was still observed and a paved area created for parking next to the retained tree groups (T088 T091) has been found since November 2012. No extension of the dumping area was noted in April 2013. As confirmed by the Project's Contractor, no construction work from the current Project has been programmed on this field and the dumping was believed to be done by parties other than the Project's Contractor.

<u>Recommendations</u>

- 3.2.6 No specific recommendation is required. However, with regard to the dumping incident on the Taro field near the Treasure Spot Garden, the Contractor is recommended to check the site condition regularly to avoid any extent of dumping or paving of area into the project boundary.
- 3.2.7 The Contractor should also make sure there are no piled rocks or construction materials influencing the nearby wetland rehabilitation area.

3.3 Contaminant/ Sediment Control

3.3.1 A series of sedimentation beds with gravels have been built along the boundary of the active works area to the south of Wai Ha and close to Tung Tsz Road in accordance with the recommendation stated in the *Monthly EM&A Report for March 2013*.

Observation

- 3.3.2 Provision of dust control measure (such as wheel washing facilities) has been maintained at two major vehicular exit points of the works area of Contract 2 (**Photo 8**).
- 3.3.3 The major construction works to the south of Tung Tsz Road was almost finished. The sedimentation beds located from north to south near the retained tree T196 (*Macaranga tanarius* var. *tomentosa*) have been established since March 2012 while another beds aligned from the area opposite to the Jade View Villa towards the marsh area at southeast have been maintained since October 2012. No muddy water was observed to be discharged into the drainage points (**Photos 9-10**).
- 3.3.4 There has been another section of sedimentation beds aligned from the area opposite to the eastern part of Jade View Villa towards the marsh area at the southeast since December 2012. The used water was released into the sedimentation beds but no heavily muddy water was observed to be discharged into the drainage point (**Photo 11**).
- 3.3.5 A new section of sedimentation bed was observed opposite to San Tau Kok with PVC liner underlying sections of granules in April 2013. The discharge is released to the marsh area and no muddy water was observed at the drainage point (**Photos 12-13**).



Drainage Improvement Works in Shuen Wan and Shek Wu Wai

Bi-weekly Landscape & Visual Monitoring

Job Ref.: 09/317/161D KLKJV -SW

EM&A (Landscape & Visual) Report (April 2013) (Issue 1)

- 3.3.6 Another section of sedimentation bed was found close to the area at which a filtration tank was previously placed opposite to San Tau Kok close to the marsh area in April 2013. PVC liner was placed underlying sections of granules and the discharge was found to be released to the marsh area. No unclear water was noted to be discharged into the drainage point (**Photo 14**).
- 3.3.7 Underground water from the built box culverts opposite to San Tau Kok was observed to be released to two drainage points at the adjacent marsh area without any filtration process as inspected on 18th April 2013 (**Photos 15-18**). It was reported to the main Contractor and no more discharge was observed during the monitoring on 30th April 2013 (**Photo 19**).
- 3.3.8 Works have been commenced in Wai Ha River since January 2013. The river was blocked by sand bags to separate the works area (**Photo 20**). The running water of the river was pumped to the end of the works area and it bypassed sections of granules down the stream (**Photo 21**).
- 3.3.9 The waste water from the construction site in Wai Ha River was pumped into a sedimentation tank placed at the end of the works area (**Photo 22**). The filtrate was then discharged to the river with several sections of granules for further sedimentation (**Photo 23**). Fences were noted to prevent the granules washing away into the stream. The discharge was found muddy at the upper section near the works area and it became cleaner after passing through several sections of granules for the sedimentation (**Photo 21**).

Recommendations

3.3.10 Regular monitoring should be conducted to ensure no direct discharge or leakage of contaminants or any polluted fluid into the adjacent Wai Ha River and the nearby Shuen Wan marsh. The Contractor should maintain regular check (e.g. daily) on the sedimentation and filtration facilities and appropriate sedimentation beds and/or tanks throughout the construction phase (e.g. check the function of the sedimentation beds and remove surplus sand and gravels deposited along the beds or within the tanks) to make sure all discharged water was filtered appropriately prior to any discharge. To prevent the impact of the unclear discharge on the nearby vegetated area, it is suggested to overlay PVC liners along the site edge and remove any surplus sand and gravels deposited in the beds and tank.

3.4 Pollution Control

3.4.1 No follow-up action by the Contractor is required as from the *Monthly EM&A Report for March 2013*.

Observation

- 3.4.2 As abovementioned, works to the south of Tung Tsz Road was almost finished. The sedimentation beds located from north to south near the retained tree T196 (*Macaranga tanarius* var. *tomentosa*) have been established since March 2012 while another beds aligned from the area opposite to the Jade View Villa towards the marsh area at southeast have been maintained since October 2012. No muddy water was observed to be discharged into the drainage points (**Photos 9-10**).
- 3.4.3 There has been another section of sedimentation beds aligned from the area opposite to the eastern part of Jade View Villa towards the marsh area at the southeast since December 2012. The used water was released into the sedimentation beds but no heavily muddy water was observed to be discharged into the drainage points (**Photo 11**).



Drainage Improvement Works in Shuen Wan and Shek Wu Wai

Bi-weekly Landscape & Visual Monitoring

Job Ref.: 09/317/161D KLKJV -SW

EM&A (Landscape & Visual) Report (April 2013) (Issue 1)

- 3.4.4 A new section of sedimentation bed was observed opposite to San Tau Kok with PVC liner underlying sections of granules in April 2013. The discharge is released to the marsh area and no muddy water was observed at the drainage point (**Photos 12-13**).
- 3.4.5 Another section of sedimentation bed was found close to the area at which a filtration tank was previously placed opposite to San Tau Kok close to the marsh area in April 2013. PVC liner was placed underlying sections of granules and the discharge was found to be released to the marsh area. No unclear water was noted to be discharged into the drainage point (**Photo 14**).
- 3.4.6 Underground water from the built box culverts opposite to San Tau Kok was observed to be released to two drainage points at the adjacent marsh area during the monitoring on 18th April 2013 (**Photos 15-18**). It was reported to the main Contractor and no more discharge was observed during the monitoring on 30th April 2013 (**Photo 19**).
- 3.4.7 Works have been commenced in Wai Ha River since January 2013. The river was blocked by sand bags to separate the works area (**Photo 20**). The running water of the river was pumped to the end of the works area and it bypassed sections of granules down the stream (**Photo 21**).
- 3.4.8 The waste water from the construction site in Wai Ha River was pumped into a sedimentation tank placed at the end of the works area (**Photo 22**). The filtrate was then discharged to the river with several sections of granules for further sedimentation (**Photo 23**). Fences were noted to prevent the granules washing away into the stream. The discharge was found muddy at the upper section near the works area and it became cleaner after passing through several sections of granules for the sedimentation (**Photo 24**).
- 3.4.9 No direct water discharge into the upper stream of Wai Ha River was observed as the active construction works have been concentrated at the lower end of Wai Ha River to the southeast of Tung Tsz Shan Road (**Photo 25**).

Recommendations

3.4.10 The Contractor should prevent any contaminants and sediments from entering the sensitive water-based habitats (i.e. Shuen Wan marsh and Wai Ha River) and implement pollution control measures to minimize any adverse environmental impacts to the water body. The Contractor should maintain appropriate sedimentation beds and/or tanks throughout the construction phase. The Contractor should adopt a good site practice in maintaining appropriate sedimentation beds and filtration tanks as recommended in the above Section for Contaminant/ Sediment Control.

3.5 Liaison with Nursery

3.5.1 The construction undertaken within Tung Tsz Nursery is restricted under Contract 1 of the Project. This monitoring item is not applicable to Contract 2 of the Project.

3.6 Existing Trees within Works Areas

3.6.1 Individual trees retained within the active works area have been protected within Tree Protection Zones (TPZs). The protection measures generally follow the recommendations stated in the *Monthly EM&A Report for March 2013*. Particular observations are highlighted in the following paragraphs.

Observation

3.6.2 No additional vegetation clearance was found in the works area.



Drainage Improvement Works in Shuen Wan and Shek Wu Wai

Bi-weekly Landscape & Visual Monitoring

Job Ref.: 09/317/161D KLKJV -SW

EM&A (Landscape & Visual) Report (April 2013) (Issue 1)

- 3.6.3 Most trees proposed to be retained within the Project Area were recorded generally in fair health conditions and some of the retained trees were naturally covered by invasive climbers.
- 3.6.4 The leaning tree T190 was still supported by the bamboo props in March 2013. Lots of creeping herbs (such as climber *Wedelia trilobata*) were found surrounding the trunk base of the tree.
- 3.6.5 Construction works at the end of the Treasure Spot Garden has commenced since October 2012. The excavation works under the drip line of the retained tree T103 was finished in January 2013. Soil was refilled to the root zone area of the tree; however, the soil was loose and sandy, and tapes and ropes were still found tied on the trunk (**Photo 26**).
- 3.6.6 The soil surface within the tree root zones of retained trees T089 and T092 has been paved with concrete since January 2013. No removal of the paved surface within the tree root zones of these two trees was noted.
- 3.6.7 No significant signs of damage on other existing tree crowns, trunks and roots resulting from the construction works were observed in this monthly monitoring.
- 3.6.8 As Area C under Contract 1 of the Project has been formally handed over to AFCD for management and maintenance since October 2012, no access into the ECA is allowed. One transplanted shrub of *Pavetta hongkongensis* (PH-03) was inspected regularly through the fence of Tung Tsz Nursery and it has remained in satisfactory condition (**Photo 27**).

Recommendations

- 3.6.9 Within the active works area, maintenance of TPZs for the retained trees and the trees to be transplanted should be continued. Trunk bases of all retained trees should be kept clear, with no stockpiled soil, construction equipments and rubbish allowed around the trunk bases and within the TPZs. If necessary, these retained trees shall be watered regularly to maintain their health. All fallen trees or tree parts of the existing trees maintained within the works area of Contract No. DC/2010/02 should be removed if they pose imminent hazards to the people/property or cause obstruction to the traffic. Any broken tree parts still attached to the trees could be pruned appropriately to prevent their potential hazard to the public and property.
- 3.6.10 Disturbance is prohibited in all TPZs. In any practical circumstances, the contractor should follow Section 8 of Annex 4 of the approved Landscape Plan for protecting the existing trees from any potential damages resulting from the construction works. In addition, the Contractor and the Project Proponent should have routine inspection on any tree remedial works conducted by other party on the trees within the Project Area.
- 3.6.11 The bamboo props for supporting the leaning tree T190 (*Ficus hispida*) should be checked regularly to ensure its efficiency in supporting the leaning trunk. The Contractor should have close monitoring of the stability of the tree and the props. If necessary, the Contractor and the Project Proponent have to restrict any access within the tree falling zone of this tree.
- 3.6.12 As there may be a risk of its overall tree stability of the retained tree T103 in the long run with regard to the potentially damaged roots within the drip line of T103, the Contractor should be aware of its stability throughout the construction phase. The taped and ropes tided on the tree trunk should be removed. If necessary, it is recommended to remove the overgrown climbers on the tree canopy so as to reduce the crown load supported by this tree.



Drainage Improvement Works in Shuen Wan and Shek Wu Wai

Bi-weekly Landscape & Visual Monitoring

Job Ref.: 09/317/161D KLKJV -SW

EM&A (Landscape & Visual) Report (April 2013) (Issue 1)

3.6.13 With regard to the tree topping incident on the retained trees T088 and T089, and the concern on the long-term tree stability of the retained tree T103, the Contractor is suggested to monitor the trees protected within the project boundary regularly. The Contractor should be aware of any potential damage on the trees by other contractor(s) undertaking construction work concurrently.

3.7 Construction Light

3.7.1 No follow-up action on maintenance of construction light is required as from the *Monthly EM&A Report for March 2013*.

Observation

3.7.2 No construction light impact to the surrounding villages and to Plover Cove as all construction activities and construction sites are halted at 1800. No construction light at night is provided by the Contractor.

Recommendation

3.7.3 No specific recommendation is required.

4 AUDIT SCHEDULE

4.1.1 The next bi-weekly Landscape & Visual Monitoring in May 2013 is scheduled to be conducted in the weeks of 13th and 27th May 2013.



Job Ref.: 09/317/161D KLKJV -SW

EM&A (Landscape & Visual) Report (April 2013) (Issue 1)

Appendix A Photographs





Photo 1 – Temporary hoardings have been erected along Tung Tsz Road opposite to Wai Ha.



Photo 2 – Temporary hoardings have been erected along the access road from Tung Tsz Road to Treasure Spot Garden II.



Photo 3 – Temporary hoardings have been erected on the path near Treasure Spot Garden II.



Photo 4 – Temporary hoardings have been extended to the northwest of the access road to Treasure Spot Garden II.



Photo 5 – The wetland rehabilitation area has been demarcated with red strings.



Photo 6 – Rocks were dumped close to the wetland rehabilitation area.



Photo 7 – Construction materials were dumped close to the wetland rehabilitation area.



Photo 8 – Wheel washing facilities has been provided at the vehicular exit point of the works area of Contract 2.



Photo 9 – The sedimentation beds and PVC liner were aligned from north to south near the retained tree T196 (*Macaranga tanarius* var. *tomentosa*) and no muddy water was discharged.



Photo 10 – The sedimentation beds with gravels and PVC liners was aligned from the area opposite to the Jade View Villa towards the marsh area at southeast.



Photo 11 – The sedimentation beds with gravels and PVC liners were aligned from the area opposite to the eastern part of Jade View Villa towards the marsh area at southeast.



Photo 12 – A new section of sedimentation bed was aligned opposite to San Tau Kok with PVC liner underlying granules in April 2013.



Photo 13 – A new section of sedimentation bed was aligned opposite to San Tau Kok with PVC liner underlying granules in April 2013. The discharge is released to the marsh area and no muddy water was observed at the drainage point.



Photo 14 – Another new section of sedimentation bed was aligned with PVC liner underlying granules close to the area at which a filtration tank was previously placed opposite to San Tau Kok close to the marsh area. The discharge is released to the marsh area. No unclear water was noted in the drainage point.



Photo 15 – Underground water was drained from the built box culverts opposite to San Tau Kok to the adjacent marsh area directly during the monitoring on 18th April 2013.



Photo 16 – Underground water from the built box culverts opposite to San Tau Kok was released to the adjacent marsh area directly during the monitoring on 18th April 2013.



Photo 17 – Underground water was drained from the built box culverts opposite to San Tau Kok to the adjacent marsh area directly during the monitoring on 18th April 2013.



Photo 18 – Underground water from the built box culverts opposite to San Tau Kok was released to the adjacent marsh area directly during the monitoring on 18th April 2013.



Photo 19 – No more discharge from the built box culverts opposite to San Tau Kok to the adjacent marsh area was observed on 30th April 2013



Photo 20 – Sand bags have been put in Wai Ha River to separate the works area in the river. The running water of the river was pumped to the end of the works area.



Photo 21 – The running water of the river was pumped to the end of the works area and it bypassed the sections of granules down the stream.



Photo 22 — The waste water from the construction site in Wai Ha River was pumped into a sedimentation tank placed at the end of the works area. The filtrate was then discharged to the river with several sections of granules for further sedimentation.



Photo 23 –The filtrate from the sedimentation tank was then discharged to the river with several sections of granules for further sedimentation.



Photo 24 – The discharge was found muddy at the upper section near the works area and it became cleaner after passing through several sections of granules for the sedimentation.



Photo 25 – No discharge of used water was observed at the upper section of Wai Ha River (i.e. to the north of Tung Tsz Shan Road).



Photo 26 – The soil refilled to the retained tree T103 was loose and sandy, and tapes and ropes were found tied on the trunk.



Photo 27 – The transplanted shrub of *Pavetta hongkongensis* (PH03) has remained in satisfactory condition in Area C under Contract 1.



Appendix M

Ecological Monitoring Report in Area under Contract 2 (No Used)
