Drainage Service Department

Monthly Environmental Monitoring & Auditing report for

Contract No.DC/2009/22 Drainage Improvement in Shuen Wan, Tai Po – Contract 1

April 2014

Environmental Pioneers & Solutions Limited
Flat A, 19/F, Chaiwan Industrial Building,
20 Lee Chung Street, Chai Wan, Hong Kong
Tel: 2556 9172 Fax: 2856 2010

Contract No. DC/2009/22 - Drainage Improvement in Shuen Wan, Tai Po - Contract I Monthly EM&A Report for April 2014

APPROVAL SHEET

The Contents of this report have been

Certified by:

Signature: 🟒 Miss. Goldie Fung

Date: 10 Jun 2014

Ecologist (Asia Ecological Consultants Ltd.)

(Environmental Team Leader)

Signature: Michael Lerra

Dr. Michael Leven (Ecologist)

Date: 28 May 2014

RLA (Environmental Resources Management)

Signature:

Date: 28/05/2014

Mr. Tai Kai Wai (RLA)

and Verified by:

IEC (ENVIRON Hong Kong Limited)

Signature:

Date: _____10 July 2014

Mr. Tony Cheng (IEC)

Environmental Pioneers & Solutions Limited

P.ii

TABLE OF CONTENT

EXI	ECUI	TIVE SUMMARY	v
1	Intr	oduction	1
2	Con	struction Stage	2
	2.1	Construction activities in the reporting period	2
	2.2	Construction activities for the coming month	2
	2.3	Environmental Status	2
3	Nois	se Monitoring	3
	3.1	Monitoring Parameters and Methodology	3
	3.2	Monitoring Equipment	3
	3.3	Monitoring Locations	4
	3.4	Monitoring Results and Interpretation	6
	3.5	Action and Limit level for Construction Noise	6
	3.6	Monitoring Schedule for the next reporting period	7
4	Wat	er Monitoring	9
	4.1	Water Quality Monitoring Parameters and Methodology	9
	4.2	Monitoring Equipment	9
	4.3	Monitoring Locations	10
	4.4	Monitoring Frequency	13
	4.5	Monitoring Results and Interpretation	13
	4.6	Action and limit level for Water Quality	14
	4.7	Monitoring Schedule for the next reporting period	20
5	Hyd	Irological Characteristics Monitoring	21
	5.1	Hydrological Characteristics Monitoring Parameters	and
	Met	hodology	21
	5.2	Monitoring Equipment	21
	5.3	Monitoring Locations	21
	5.4	Monitoring Frequency	23
	5.5	Monitoring Results and Interpretation	23
	5.6	Action and limit level for Hydrological Characteristics	23
	5.7	Monitoring Schedule for the next reporting period	27
6	Ecol	logical Monitoring of ECA	28
	6.1	Ecological Monitoring of ECA	28
	6.2	Monitoring Results	28
7	Lan	dscape and Visual	30
	7.1	Introduction	30
	7.2	Scope of Monitoring	30

	7.3 Landscape and Visual Monitoring Results	
	7.4 Audit Schedule	45
8	Action taken in Event of Exceedance	46
9	Construction waste disposal	47
10	Status of Permits and Licenses obtained	50
11	Compliant Log	51
12	Site Environmental Audits	51
	12.1 Site Inspection	51
	12.2 Compliance with legal and Contractual requirement	52
	12.3 Implementation status and effectiveness of the mitigation	on measures
	52	
13	Future Key issues and recommendations	52
14	Conclusions	

LIST OF APPENDIXES

Appendix A: Site Location
Appendix B: Key Personal Contact information chart
Appendix C: Calibration Certificates for measuring instruments
Appendix D: Construction Noise Monitoring Data
Appendix E: Water Quality Monitoring Data
Appendix F: Hydrological Characteristics Monitoring Data
Appendix G: Landscape and Visual Monitoring Photos
Appendix H: Implementation status of environmental protection and mitigation
measures
Appendix I: Construction programme
Appendix J: Three month rolling programme
Appendix K: Graphical plots of trends of monitored parameters
Appendix L: Photo of Wai Ha River in April 2014

EXECUTIVE SUMMARY

This is the thirty eighth monthly Environmental Monitoring and Audit (EM&A) Report for the drainage improvement works in Shuen Wan, Tai Po under Drainage Services Department Contract No. DC/2009/22 entitled "Drainage Improvement Works in Shuen Wan, Tai Po – Contract 1". This report concludes the impact monitoring for the activities undertaken during the period from 1^{st} April 2014 to 30^{th} April 2014. The major site activities in this reporting period were mainly rectification works at Ting Kok Road, remaining works at intake structure and reinstatement in Tung Tzs Nursery.

The Environmental Team (ET) is responsible for the EM&A works required in the EM&A manual (revision 3). Site inspections were carried out on weekly basis to investigate and audit the equipment and work methodologies with respect to pollution control and environmental mitigation. The weekly inspections records and photos taken were kept.

In general, waste management was satisfactory during the reporting period.

Impact monitoring for construction noise was conducted in the reporting period. No exceedance of A/L level was reported.

Furthermore, impact monitoring for water quality was conducted. Total 11 abnormal incidents of water quality criteria were recorded in this reporting month. During the reporting period, no construction activities were conducted near the Wai Ha River. Proper mitigation measures were implemented by contractor to avoid site water releasing to the Wai Ha river and no particular observation of defective site activities were found causing water contamination. The exceedances of Turbidity and SS were believed to be mainly attributed by natural fluctuation and adverse weather. And, since the recorded levels of Turbidity and SS at control station had also exceeded its baseline action or limit level, the exceedances recorded at W2 were unlikely to be related to the Project.

No exceedance of A/L level was reported for the monitoring of hydrological characteristics in the reporting period.

The ECA was handed over to AFCD on 16th October 2012. And, the monitoring for Pavetta hongkongensis was completed.

Visual and landscape monitoring has been conducted for the project. Details of the observations are referred to sections 7.

There was no complaint, notification of any summons and successful prosecutions against the project received during the reporting period.

Site works proposed to be carried out in the upcoming month at Area A & B are refer to section 2.2.

It is expected that noise, air and water quality impacts will be resulted from the works. ET has reminded the contractor to provide environmental pollution control measures wherever necessary and to keep a good environmental management at site practice. The recommended mitigation measures proposed for the project as well as implementation status are refer to section 12.3.

The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual (revision 3) and Environmental Permit requirement.

1 Introduction

This is the thirty eighth monthly Environmental Monitoring and Audit (EM&A) Report for the drainage improvement works in Shuen Wan, Tai Po under Drainage Services Department Contract No. DC/2009/22 entitled "Drainage Improvement Works in Shuen Wan, Tai Po – Contract 1". The site layout plan is shown in **Appendix A**. The Environmental Team, Environmental Pioneers & Solutions Limited was appointed by Kwan Lee – Kuly Joint Venture to prepare the report. The report is to be submitted to the Contractor, the Engineer and the IEC.

This report presents the results of the environmental monitoring of the project activities conducted within the reporting period from 1st April 2014 to 30th April 2014. This report included the noise monitoring, water quality monitoring, hydrological characteristics monitoring, visual and landscape monitoring, and regular site inspections once per week for verification of implementation of the mitigation measures as recommended in the Environmental Permit (EP-303/2008) (EP), EM&A Manual (revision 3) and the Contractor's Environmental Management Plan (EMP).

2 Construction Stage

2.1 Construction activities in the reporting period

Major activities in the reporting period included the followings:

Area A.:

- Rectification works at Ting Kok Road
- Remaining works at Intake Structure

Area B.:

- Reinstatement in Tung Tsz Nursery

2.2 Construction activities for the coming month

Proposed key construction works in the coming months will include:

Area A (Pumping Station)

- 1. Rectification works at Ting Kok Road
- 2. Remaining works at Intake Structure

Area B (Tung Tsz Nursery)

1. Reinstatement in Tung Tsz Nursery

2.3 Environmental Status

Appendix A shows the drawing of the project area.

Locations of the monitoring and control stations with environmental sensitive receivers are presented in Section 3.3, 4.3, and 5.3 for noise, water quality, and hydrological characteristics respectively.

3 Noise Monitoring

3.1 Monitoring Parameters and Methodology

The construction noise level was measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). $L_{eq (30minutes)}$ was used as the monitoring parameter for the impact monitoring in the time period between 0700 to 1900 hours on normal weekdays. For all other time period, $L_{eq (5minutes)}$ was employed for comparison with the Noise Control Ordinance (NCO) criteria.

Noise measurement results obtained from each monitoring location were recorded in the Construction Noise Monitoring Data Sheet (**Appendix D**) immediately after the measurement. As supplementary information for data auditing, statistical results L_{10} and L_{90} were also be recorded for reference.

In case of non-compliance with the construction noise criteria, more frequent monitoring, as specified in the Action plan in Table 3.5.2, shall be carried out. This additional monitoring shall be carried out until the recorded noise levels are rectified or proved to be irrelevant to the construction activities.

3.2 Monitoring Equipment

The sound level meters and calibrators comply with the International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications as referred to in the Technical Memorandum (TM) to the Noise Control Ordinance was deployed as monitoring equipment for noise measurement.

Noise measurement was not be made in the presence of fog, rain, wind with a steady speed exceeding 5ms⁻¹ or wind with gust exceeding 10ms⁻¹. Thus wind speed was checked by the portable wind speed indicator capable of measuring the wind speed in m/s. Table 3.2.1 summarizes the equipment list for noise monitoring

E automat							
Equipment	Manufacturer & Model No.	Precision Grade	Qty				
Integrated sound	Svantek 955	IEC 61672 Type 1	1				
level meter		IEC 1260 Type 1					
Windscreen	Microtech gefell model W2	N/A	1				
Acoustical	Svantek SV30A	IEC 942 Type 1	1				
calibrator							
Wind speed	Kestrel K1000	N/A	1				
indicator							
Remarks: Calibration details of the sound level meter is given in Appendix C for							
reference							

Table 3.2.1 E	Equipment List for	Noise Monitoring
---------------	--------------------	------------------

3.3 Monitoring Locations

According to the Environmental Monitoring and Audit manual, impact noise monitoring for contract 1 was undertaken at two locations during the construction phase of the project. The proposed monitoring locations are summarized in Table 3.3.1. Figure 3.3.1 shows the Noise Monitoring Locations.

Noise measurement at each monitoring location was taken at a point 1m from the exterior of the selected premises and at a height of 1.2m above ground with no disturbance to the dweller and least obstructed view.

Noise Station	Monitoring	Location
M1		14, Shuen Wan Chim Uk
AL1		Joint Village Office for Villages in Shuen Wan, Tai Po

Table 3.3.1 Noise Monitoring Locations during Construction Phase

In accordance with the requirements in the EM&A manual (revision 3), weekly impact monitoring was conducted. For the time period between 0700 and 1900 hours on normal weekdays, and noise parameter of $L_{eq (30minutes)}$ was measured. As if the construction works were carried out during restricted period (i.e. 1900-2300, 2300-0700 of next day and Sundays / general holiday), impact monitoring that comprises 3 consecutive $L_{eq (5minutes)}$ would be carried out.

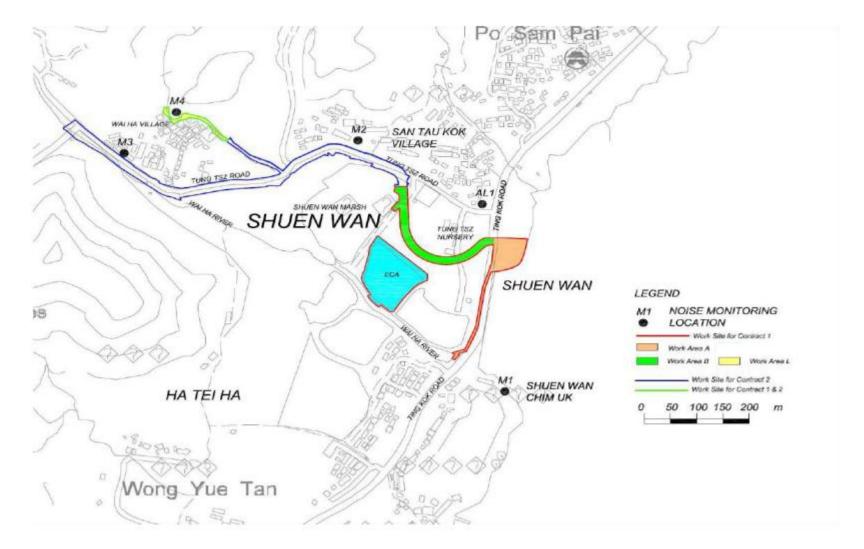


Figure 3.3.1 Impact noise monitoring locations

3.4 Monitoring Results and Interpretation

Relevant details of the noise monitoring results are presented in Table 3.4.1. The results of M1 ranged between 62.3dB (A) and 64.5dB (A), and AL1 ranged between 66.7dB (A) and 69.7dB (A), were within the limit levels and therefore, no exceedance was found.

Table 3.4.1 Noise Monitoring Results for the reporting period							
Location	Parameter	Date*	Time	L _{Aeq} dB(A)	Limit dB(A)	Exceedance	Weather
M1	Leq 30mins	2-Apr-14	9:25	64.5	75	Ν	Cloudy
M1	Leq 30mins	9-Apr-14	9:50	63.3	75	Ν	Sunny
M1	Leq 30mins	16-Apr-14	9:30	62.5	75	Ν	Sunny
M1	Leq 30mins	23-Apr-14	14:00	62.3	75	Ν	Cloudy
M1	Leq 30mins	30-Apr-14	14:30	64.5	75	Ν	Sunny
AL1	Leq 30mins	2-Apr-14	10:05	69.7	75	Ν	Cloudy
AL1	Leq 30mins	9-Apr-14	10:45	68.8	75	Ν	Sunny
AL1	Leq 30mins	16-Apr-14	10:05	66.7	75	Ν	Sunny
AL1	Leq 30mins	23-Apr-14	14:40	67.8	75	Ν	Cloudy
AL1	Leq 30mins	30-Apr-14	15:05	68.7	75	Ν	Sunny

Remarks: Raw datasheet for noise monitoring are attached in **Appendix D** for reference.

3.5 Action and Limit level for Construction Noise

The Action and Limit (A/L) levels for construction noise are defined in Table 3.5.1. Should non-compliance of the criteria occur, action in accordance with the Action Plan in Table 3.5.2 should be carried out.

There was no exceedance recorded in the reporting period.

Table 3.5.1 Action and Limit Levels for Construction noise

Time Period	Action Level	Limit Level			
	When one documented complaint is received	75dB(A)			
Remarks: If	works are to be carried out du	ring restricted hours, the			
conditions st	ipulated in the construction no	ise permit issued by the			
Noise Control Authority have to be followed.					

3.6 Monitoring Schedule for the next reporting period

Noise monitoring schedule is proposed to be carried out on,7th, 14th, 21st and 28th of May 2014.

EVENT	ET Leader	IEC	ER	CONTRACTOR	
Action	1. Notify IEC	1. Review the	1. Confirm	1. Submit	
Level	and	analysed	receipt of	noise	
	Contractor.	results	notification	mitigation	
	2. Carry out	submitted	of	proposals to	
	investigation.	by the ET.	f	IEC.	
	3. Report the	2. Review the	ailure in	2. Implement	
	results of	proposed	writing.	noise	
	investigation	remedial	2. Notify	mitigation	
	to the IEC,	measures by	Contractor.	proposals.	
	ER and	the	3. Require		
	Contractor.	Contractor	Contractor		
	4. Discuss with	and advise	to propose		
	the	the ER	remedial		
	Contractor	accordingly.	measures		
	and formulate	3. Supervise	for the		
	remedial	the	analysed		
	measures.	implementat	noise		
	5. Increase	ion of	problem;		
	monitoring	remedial	4. Check		
	frequency to	measures.	remedial		
	check		measures		

Table 3.5.2 Event / Action Plan for Construction Noise

Limit	1. Notify IEC,	1. Discuss	1. Confirm	1. Take
Level	ER, EPD and	amongst	receipt of	immediate
	Contractor.	ER, ET, and	notification	action to
	2. Identify	Contractor	of	avoid
	source.	on the	f	2. Submit
	3. Repeat	potential	ailure in	proposals
	measurement	remedial	writing.	for remedial
	s to confirm	actions.	2. Notify	actions to
	findings.	2. Review	Contractor.	IEC within
	4. Increase	C ontractor'	3. Require	3 working
	monitoring	s' remedial	Contrac	days of
	frequency.	actions	tor to	notification.
	5. Carry out	whenever	propose	3. Implement
	analysis	necessary to	remedial	the
	of	assure their	measures	agreed
	Contractor's	effectivenes	for the	proposals.
	working	s and	analysed	4. Resubmit
	procedures to	advis	noise	proposals if
	determine	e the	problem.	problem still
	possible	3. Supervise	4. Check	not under
	mitigation to	the	remedial	control.
	be	implementat	measures	5. Stop the
	implemented.	ion of	properly	relevant
	6. Inform IEC,	remedial	implemente	portion of
	ER and EPD	measures.	d.	works as
	the causes		5. If	determined
	and actions		exceedance	by the
	taken for the			ER until the
	exceedances.			exceedance
	7. Assess			is abated.
	effectiveness			
	of			
	Contractor's			
	remedial			
	actions and			
	keep IEC,			
	EDD and ED			

4 Water Monitoring

4.1 Water Quality Monitoring Parameters and Methodology

Turbidity in Nephelometric Turbidity Unit (NTU), and Dissolved Oxygen (DO) in mg/L, temperature, and pH measurements were in-situ measurements and suspended solids measurements were performed by a HOKLAS accredited laboratory using recommended reference method APHA 2540D.

4.2 Monitoring Equipment

Turbidity, DO, Salinity, pH and temperature was measured by an instrument complied with the following requirements:

The instrument is a portable as well as weatherproof multimeter complete with cable and uses a DC power source. It is capable of measuring:

- A turbidity between 0-800NTU;
- A dissolved Oxygen level in the range of 0-20mg/L and 0-200% saturation;
- A temperature of 0-50°C;
- Salinity in the range of 0-40ppt;
- pH in the range of 0-14.

The measurements were performed by a portable and weatherproof multi-meter, model TOA-DKK WQC-24. The equipment was calibrated and verified by certified laboratory every 3 months to ensure they perform to the same level of accuracy as stated in the manufacturer's specification. Detailed calibration records of the multi-meter were shown in **Appendix C** for reference

Suspended solids were determined by the water samples collected from the monitoring locations for further analysis in accredited HOKLAS laboratory. Water samples were contained by polythene bottles, packed in ice (cooled in 4°C without frozen) and delivered to the laboratory for analysis as soon as possible after collection.

4.3 Monitoring Locations

In accordance with the EM&A Manual (revision 3), monitoring stations for contract 1 were established at two locations, which are summarized in Table 4.3.1.

Monitoring Station	Location	Coordinates
W1	Between the Shuen Wan Marsh	E:839301
vv 1	and ECA	N:836386
wo	Between Tolo Harbour and	E:839542
W2	Proposed Penstock	N:836184

Table 4.3.1 – Water Quality Monitoring Stations

As illustrated in Figure 4.3.1, W1 served as the control station while W2 was the monitoring location of water quality.

According to the approved proposal of revision for Action/Limit Level Criteria of Water Quality Monitoring, two reference points (C1 & C2) were added.

Should the water quality parameters monitoring results at the monitoring station W2 exceed the water quality criteria, the water quality monitoring data of two reference points (C1 and C2) will be used as the supplementary information. The monitoring data of C1 should be used for comparison with the monitoring data of W2 that taken at flood tide; and the monitoring data of C2 should be used for comparison with the monitoring data of W2 that taken at ebb tide. The comparison of water quality between W2 and C1 at flood tide and between W2 and C2 at ebb tide is to prove whether influence of water quality is caused by the construction activities. The details of C1 and C2 are referred to the previous submission.

In accordance with the EM&A Manual (revision 3), measurements shall be taken at 3 water depths, namely, 1m below water surface, mid-depth and 1m above river bed, except where the water depth less than 6m, the mid-depth station may be omitted. Should the water depth be less than 3m, only the mid-depth station will be monitored. As the depth of water was less than 3m, water samples were collected at mid-depth of each proposed monitoring stations for measurements and sample collection.

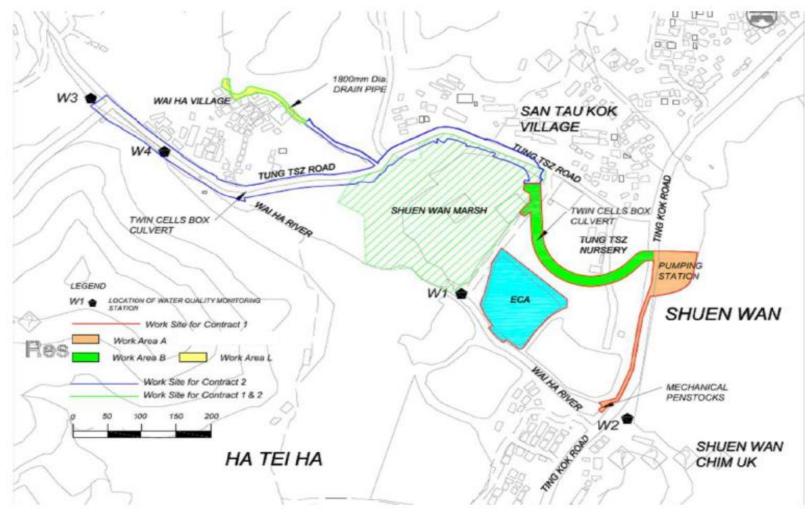


Figure 4.3.1 Water Quality Monitoring Locations

4.4 Monitoring Frequency

Impact water quality monitoring for each monitoring station were performed at mid-flood or mid-ebb tides for 3 days per week during the course of the construction river works.

Monitoring was carried out on 2^{nd} , 4^{th} , 7^{th} , 9^{th} , 11^{th} , 14^{th} , 16^{th} , 23^{rd} , 25^{th} , 28^{th} and 30^{th} of April 2014.

4.5 Monitoring Results and Interpretation

Water quality monitoring was carried out eleven times in this reporting month. Detailed on-site measurements are shown in **Appendix E**. Table 4.5.1 presents consolidated results throughout the reporting month.

There were 11 abnormal incidents of water quality limits (Turbidity) were recorded in this reporting month according to the established action and limit levels. ET has arranged site investigations for the abnormal incidents. No construction activities were carried out at the river bed. During the reporting period, no construction activities were conducted near the Wai Ha River. Proper mitigation measures were implemented by contractor to avoid site water releasing to the Wai Ha river and no particular observation of defective site activities were found causing water contamination. The exceedances of Turbidity and SS were believed to be mainly attributed by natural fluctuation and adverse weather. And, since the recorded levels of Turbidity and SS at control station had also exceeded its baseline action or limit level, the exceedances recorded at W2 were unlikely to be related to the Project.

The water condition of Wai Ha River is presented in photo attached in **Appendix M.**

	Average of M	Average of Monitoring Results					
	Temperature (°C)	Turbidity (NTU)	pH	Dissolved Oxygen (mg/L)	Dissolved Oxygen (%)	Suspended Solids (mg/L)	
W1	23.5	5.8	6.81	6.76	78.2	4.1	
W2	21.1	8.6	7.93	7.92	86.8	4.8	
C1	21.6	3.55	8.13	8.31	100.0	2.3	
C2	23.6	7.2	7.33	7.21	84.3	2.4	

Table 4.5.1 Summary of Water Quality Monitoring Results of this reporting month

Date	Tide	Parameter	Interpretations
2/4/2014	Mid-ebb	Turbidity	
2/ 4/ 2014	Wild-COU	SS	
4/4/2014	Mid-ebb	Turbidity	
7/4/2014	Mid-ebb	Turbidity	
9/4/2014	Mid-flood	Turbidity	
11/4/2014	Mid-ebb	Turbidity	Exceedance was caused by natural fluctuation
14/4/2014	Mid-ebb	Turbidity	and adverse weather
16/4/2014	Mid-ebb	Turbidity	
23/4/2014	Mid-flood	Turbidity	
25/4/2014	Mid-flood	Turbidity	
28/5/2014	Mid-ebb	Turbidity	
30/4/2014	Mid-ebb	Turbidity	

4.6 Action and limit level for Water Quality

Based on the criteria stipulated in EM&A manual (revision 3) and baseline water quality monitoring data obtained, the A/L levels are shown in Table 4.6.1, Table 4.6.2. The A/L levels for W1 were ignored since W1 functions as the control station for contract 1. If the water quality monitoring results at any

impact stations exceeded the criteria, the actions in accordance with the Event and Action Plan in Table 4.6.3 should be taken.

Parameters	Action	Limit
DO in mg/L	5 percentile of baseline data	4 mg/L
pН	N/A	6.0 - 9.0
SS in mg/L	95 percentile of baseline data or 120% of upstream control	99 percentile of baseline data or 130% of upstream control
Turbidity in NTU	station's SS 95 percentile of baseline data or 120% of upstream control station's Turbidity	station's SS 99 percentile of baseline data or 130% of upstream control station's Turbidity

Table 4.6.1 Action and Limit Levels for Water Quality at All Monitoring Stations

Table 4.6.2	Action and	l imit Levels fo	r Water C	Juality at All	Monitoring Stations
14010 4.0.2	Action and			zuanty at An	monitoring stations

	Monitoring Stations (Flood Tide)) Monitoring Stations (Ebb Tide)			
Davamatara	W	/1	W	/2	W	/1	W2	
Parameters	Action	Limit	Action	Limit	Action	Limit	Action	Limit
	Level	Level	Level	Level	Level	Level	Level	Level
DO (mg/L)	8.07	8.07	7.81	7.69	7.12	7.02	6.77	6.31
pН	N/A	6.0-9.0	N/A	6.0-9.0	N/A	6.0-9.0	N/A	6.0-9.0
SS (mg/L)	7.7	8.1	7.7	8.6	10.5	10.9	9.4	9.9
Turbidity (NTU)	4.9	5.3	1.7	1.8	4.2	4.7	3.0	3.5

Remarks:

For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits

For SS and turbidity, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

Event	ET Leader	IEC	ER	Contractor
ACTION LE	VEL			
Action	1. Repeat in-situ	1. Discuss	1. Discuss	1. Inform
level being	measurement	mitigation	proposed	Engineer and
exceeded	s to confirm	measures	mitigation	confirm in
by one	findings;	with ET,	, measures	writing
sampling	2. Identify	Engineer	with IEC	notification
day	reasons for	and	ET and	of the
	non-complian	Contractor;	Contractor	non-complian
	ce and	2. Review	;	ce;
	source(s) of	proposals on	2. Make	2. Rectify
	impact;	mitigation	agreement	unacceptable
	3. Inform IEC,	, measures	on	practice;
	Contractor	submitted	mitigation	3. Check all
	and Engineer;	by	measures	plant and
	4. Check	Contractor	to be	equipment;
	monitoring	and advise	e implement	4. Consider
	data, all plant	, the Engineer	ed;	changes in
	equipment	accordingly;	3. Assess	working
	and	3. Assess	effectivene	methods;
	Contractor's	effectivenes	ss of	5. Discuss with
	working	s of	implement	ET, IEC and
	methods;	implemente	ed	Engineer and
	5. Discuss	d mitigation	mitigation	propose
	mitigation	measures.	measures.	mitigation
	measures			measures to
	with IEC,	,		IEC and
	Engineer and	l		Engineer
	Contractor;			within three
	6. Ensure			working
	mitigation			days;
	measures are			6. Implement
	implemented.			agreed
				mitigation
	Repeat			measures.
	measurement on			
	next day of			

Table 4.6.3 Event and action Plan for Water Quality

	exceedance.			
Action level being exceeded	s to confirm	mitigation measures	proposed mitigation	Inform Engineer and confirm in
by more	e,	with ET,	measures	writing
than two	2	Engineer	with IEC,	notification
consecutive	reasons for	and Contractor;	ET and Contractor	of the
sampling days	non-complian ce and	2. Review	·	non-complian ce;
days	source(s) of	proposals on	, 2. Make 2.	,
	impact;	mitigation	agreement	unacceptable
	3. Inform IEC,	measures	on	practice;
	Contractor	submitted	mitigation 3.	Check all
	and Engineer;	by	measures	plant and
	4. Check	Contractor	to be	equipment;
	monitoring	and advise	implement 4.	Consider
	data, all plant,	the Engineer		changes in
	equipment	accordingly;		working
	and	3. Assess	effectivene	methods;
	Contractor's	effectivenes	ss of 5.	
	working	s of	1	ET, IEC and
	methods;	implemente	ed	Engineer and
	5. Discuss	d mitigation	C	propose
	mitigation	measures.	measures.	mitigation
	measures			measures to
	with IEC,			IEC and
	Engineer and Contractor;			Engineer within three
	6. Ensure			working
	mitigation			days;
	measures are		6.	-
	implemented.			agreed
	7. Prepare to			mitigation
	increase the			measures.
	monitoring			
	frequency to			
	daily;			

	0 D (
	8. Repeat			
	measurement			
	on next day			
	of exeedance.			
LIMIT LEV				
Limit level	1. Repeat in-situ	1. Discuss	1. Discuss	1. Inform
being	measurements	mitigation	proposed	Engineer and
exceeded	to confirm	measures	mitigation	confirm in
by one	findings;	with ET,	measures	writing
sampling	2. Identify reasons	Engineer	with IEC,	notification
day	for	and	ET and	of the
	non-complianc	Contractor;	Contractor	non-complian
	e and source(s)	2. Review	;	ce;
	of impact;	proposals on	2. Request	2. Rectify
	3. Inform EPD,	mitigation	Contractor	unacceptable
	IEC,	measures	to	practice;
	Contractor and	submitted	critically	3. Check all
	Engineer;	by	review the	plant and
	4. Check	Contractor	working	equipment;
	monitoring	and advise	methods;	4. Consider
	data, all plant,	the Engineer	3. Make	changes in
	equipment and	accordingly;	agreement	working
	Contractor's	3. Assess	on	methods;
	working	effectivenes	mitigation	5. Discuss with
	methods;	s of	measures	ET, IEC and
	5. Discuss	implemente	to be	Engineer and
	mitigation	d mitigation	implement	propose
	measures with	measures.	ed;	mitigation
	IEC, Engineer		4. Assess	measures to
	and		effectivene	IEC and
	Contractor;		ss of	Engineer
	6. Ensure		implement	within three
	mitigation		ed	working
	measures are		mitigation	days;
	implemented;		measures.	6. Implement
	7. Increase the			agreed
1 1	monitoring			mitigation

	frequency to			measures.
	daily until no			
	exceedance of			
	Limit level.			
Limit level	1. Repeat in-situ 1.	Discuss	1. Discuss 1	1. Inform
being	measurements	mitigation	proposed	Engineer and
exceeded	to confirm	measures	mitigation	confirm in
by more	findings;	with ET,	e	writing
than two	2. Identify reasons	Engineer	with IEC,	notification
consecutive	for	and	ET and	of the
sampling	non-compliance	Contractor;	Contractor	non-complian
days	and source(s) of 2.	,		ce;
days	impact;	proposals on	, 2. Request 2	2. Rectify
	3. Inform EPD,	mitigation	Contractor	unacceptable
	IEC, Contractor	measures	to	practice;
	and Engineer;	submitted		3. Check all
	4. Check	by	review the	plant and
	monitoring	Contractor	working	equipment;
	data, all plant,	and advise	U	4. Consider
	equipment and	the Engineer	,	changes in
	Contractor's	accordingly;		working
		Assess	on	methods;
	methods;	effectivenes	_	5. Discuss with
	5. Discuss	s of	-	ET, IEC and
	mitigation	implemente	to be	Engineer and
	measures with	d mitigation		propose
	IEC, Engineer	measures.	ed;	mitigation
	and Contractor;	measures.	4. Assess	measures to
	6. Ensure		effectivene	IEC and
	mitigation		ss of	Engineer
	measures are		implement	within three
	implemented.		ed	working
	7. Increase the		mitigation	days;
	monitoring		-	5. Implement
	frequency to		5. Consider	agreed
	daily until no		and if	mitigation
	exceedance of		necessary	measures;
			neeessary	measures,

Г		r				
Limit level for	instruc	t	7.	As	dire	cted
two consecutive	Contra	ctor		by		the
days.	to	slow		Engi	neer,	
	down	or to		slow	dow	n or
	stop a	ll or		stop	all	or
	part of	f the		part	of	the
	constru	ictio		const	ructi	on
	n activ	vities		activ	ities	
	until	no		until		no
	exceed	lanc		excee	edanc	e
	e of L	imit		of	L	imit
	Level.			level	•	

4.7 Monitoring Schedule for the next reporting period

Water quality monitoring schedule is proposed to be carried out on 2nd, 5th, 7th, 9th, 12th, 14th, 16th, 19th, 21st, 23rd, 26th, 28th and 30th of May 2014.

5 Hydrological Characteristics Monitoring

5.1 Hydrological Characteristics Monitoring Parameters and Methodology

Impact monitoring of hydrological characteristics was undertaken to establish hydrological characteristics of sections of Wai Ha River adjacent to Drainage Improvement Works in Shuen Wan, Tai Po.

The hydrological characteristics of sections of Wai Ha River were measured by water flow rate and depth.

5.2 Monitoring Equipment

Monitoring performed by a portable echo-sounder, model Greyline Stingray. The equipment was calibrated and verified by certified laboratory or manufacturer every year to ensure they perform to the same level of accuracy as stated in the manufacturer's specification.

Calibration Certificate of the multi-meter is given in Appendix C.

5.3 Monitoring Locations

In accordance with the EM&A Manual (revision 3), monitoring stations for contract 1 were established at two locations and summarized in Table 5.3.1.

Monitoring Station	Location	Coordinates
H1	Between the Shuen Wan Marsh	E:839301
	and ECA	N:836386
H2	Route to Sam Kung Temple	E:839163
		N:836433

Table 5.3.1 – Water Quality Monitoring Stations

As illustrated in Figure 5.3.1, H2 served as the control station while H1 was the monitoring location of hydrological characteristics.

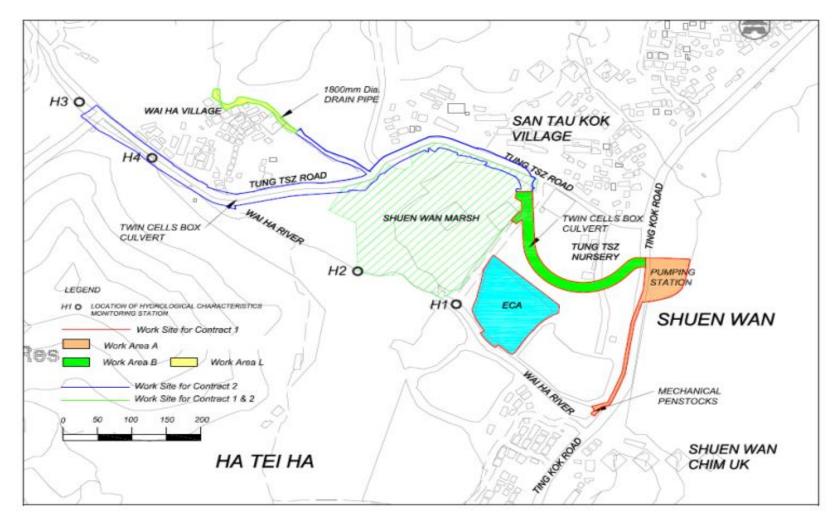


Figure 5.3.1 Hydrological Characteristics Monitoring Locations

5.4 Monitoring Frequency

Hydrological characteristics monitoring for each monitoring station were performed at mid-flood and mid-ebb tides for once per week during the course of the construction river works.

Monitoring was carried out on 4th, 11th, 16th and 25th of April 2014.

5.5 Monitoring Results and Interpretation

Hydrological characteristics monitoring was carried out four times in this reporting period. The monitoring results are summarized in Table 5.5. All results were within the action and limit levels, therefore, no exceedance was found.

	Average of Monitoring	Average of Monitoring Results				
	Water Depth (m)	Water Flow Rate (m ³ /s)				
H1(Flood)	~0.340	~0.131				
H1(Ebb)	~0.195	~0.169				
H2(Flood)	~0.360	~1.036				
H2(Ebb)	~0.240	~1.319				

Table 5.5Summary of Water Quality Monitoring Results

Details of the monitoring data were presented in Appendix F.

5.6 Action and limit level for Hydrological Characteristics

The Action and Limit levels for all monitoring stations are summarized in Table 5.6.1, which would be applied for compliance assessment of hydrological characteristics for this project. If the hydrological characteristics monitoring results at any impact stations exceeded the criteria, the actions in accordance with the Event and Action Plan in Table 5.6.2 should be taken.

Table	5.6.1	Action	and	Limit	Levels	for	Hydrological	Characteristics	at	All
Monite	oring S	Stations								

Parameters	Action	Limit		
Water Depth at	0.08	0.06		
Mid-flood (m)	0:08			
Water Depth at	0.08	0.06		
Mid-ebb (m)	0.08			
Water Flow	120% of control station's	140% of control station's water		
Water Flow Rate (m^3/s)	water flow rate on the same	flow rate on the same day of		
Kate (III /S)	day of measurement	measurement		

Event		Leader		ER	Cont	ractor
			IEC	CK	Cont	ractor
ACTION LE			1 D'	1. D'	1	T C
Action	1.	Repeat in-situ		1. Discuss	1.	Inform
level being	5	measurements to	U	proposed		Engineer and
exceeded	2	confirm findings;	measures with	U		confirm in
by one	2.	Identify reasons	, U			writing
sampling		for	and	with IEC.	,	notification of
day		non-compliance	Contractor;	ET and		the
		and source(s) of		Contractor;		non-complian
	2	impact;	proposals on		2	ce;
	3.	Inform IEC,	mitigation	agreement	2.	Rectify
		Contractor and	measures	on		unacceptable
	4	Engineer;	submitted by	U	2	practice;
	4.	Check monitoring		measures		Check
		data, Contractor's				working
		working methods	U	implemente		methods and
		and any	accordingly;	d;		any
		excavation works		3. Assess		excavation
		or dewatering		effectivene		works or
	5	processes;	of	ss of		dewatering
	5.	Discuss	implemented	implemente		processes;
		mitigation	mitigation	d miti soti on	4.	Consider
		measures with		mitigation		changes in
		IEC, Engineer		measures.		working
	~	and Contractor;				methods and
	6.	Ensure mitigation			~	plans;
		measures are			5.	Discuss with
	7	implemented.				ET, IEC and
	7.	Repeat				Engineer and
		measurement on				propose
		next day of exceedance.				mitigation
		exceedance.				measures to IEC and
						Engineer within three
					6	working days;
					6.	Implement
						agreed
						mitigation measures.
Action	1	Donast in site	1. Discuss	1. Discuss	1	Inform
	1.	Repeat in-situ			1.	
level being exceeded	5	measurements to confirm findings;	mitigation measures with	proposed mitigation		Engineer and confirm in
by more	2	Identify reasons		U		confirm in writing
than two		for	and	with IEC.		notification of
consecutive			Contractor;	ET and	,	the
		non-compliance and source(s) of	· · · · · ·			
sampling				Contractor;		non-complian
days	2	impact;	proposals on		2	ce; Doctify
	3.	Inform IEC,	mitigation	agreement	2.	Rectify

		~ 1			
		Contractor and	measures	on	unacceptable
		Engineer;	submitted by	mitigation	practice;
	4.	Check monitoring	Contractor	measures	3. Check
		data, Contractor's	and advise the	to be	working
		working methods	Engineer	implemente	methods and
		and any	accordingly;	d;	any
		excavation works	3. Assess	3. Assess	excavation
		or dewatering	effectiveness	effectivene	works or
		processes;	of	ss of	dewatering
	5.	Discuss	implemented	implemente	processes;
	5.	mitigation	mitigation	d	4. Consider
		measures with	measures.	mitigation	
			measures.	-	U
		IEC, Engineer		measures.	working
	~	and Contractor;			methods and
	6.	Ensure mitigation			plans;
		measures are			5. Discuss with
	_	implemented.			ET, IEC and
	7.	Prepare to			Engineer and
		increase the			propose
		monitoring			mitigation
		frequency to			measures to
		daily;			IEC and
	8.	Repeat			Engineer
		measurement on			within three
		next day of			working days;
		exeedance.			6. Implement
					agreed
					mitigation
					measures.
LIMIT LI	EVE	L			
Limit level	1.	Repeat in-situ	1. Discuss	1. Discuss	1. Inform
being		measurements to	mitigation	proposed	Engineer and
exceeded		confirm findings;	measures with	mitigation	confirm in
by one	2.	Identify reasons	ET, Engineer	measures	writing
sampling		for	and	with IEC,	notification of
day		non-compliance	Contractor;	ET and	the
		and source(s) of	2. Review	Contractor;	non-compliance
		impact;	proposals on	2. Request	;
	3.	Inform AFCD,	mitigation	Contractor	2. Rectify
		IEC, Contractor	measures	to critically	unacceptable
		and Engineer;	submitted by	review the	practice;
	4.	Check monitoring	Contractor	working	3. Check working
		data, and	and advise the	methods;	methods and
		Contractor's	Engineer	3. Make	any excavation
		working methods	accordingly;	agreement	works or
		and any	3. Assess	on	dewatering
		excavation works	effectiveness	mitigation	processes;
		or dewatering	of	measures	4. Consider
		processes;	implemented	to be	changes in
	5.	Discuss	mitigation	implemente	working
	5.	100000	muganon	implemente	working

		mitigation	maggurag		d;		methods	and
		-	measures.	4	u, Assess			and
				4.		5	plans;	th
		IEC, Engineer			effectivene	Э.		with
	\mathbf{c}	and Contractor;			ss of		,	and
	6.	Ensure mitigation			implemente		U	and
		measures are			d		propose	
	7	implemented;			mitigation		mitigation	
	7.	Increase the			measures.		measures to 1	
		monitoring					and Engir	
		frequency to daily						nree
		until no					working days	s;
		exceedance of				6.	. Implement	
		Limit level.					agreed	
							mitigation	
							measures.	
Limit level	1.	1	1. Discuss	1.	Discuss	1.	Inform	-
being		measurements to	mitigation		proposed		0	and
exceeded	-	confirm findings;	measures with		mitigation		confirm	in
by more		Identify reasons	ET, Engineer		measures		writing	
than two		for	and		with IEC,		notification	of
consecutive		non-compliance	Contractor;		ET and		the	
sampling		and source(s) of		-	Contractor;		non-complia	nce
days	_	impact;	proposals on	2.	Request		;	
	3.	Inform AFCD,	mitigation			2.	Rectify	
		IEC, Contractor	measures		to critically		unacceptable	e
		and Engineer;	submitted by		review the		practice;	
	4.	Check monitoring	Contractor		working	3.	Check work	_
		data, and	and advise the		methods;			and
		Contractor's	Engineer	3.	Make		any excavat	tion
		working methods	accordingly;		agreement		works	or
		and any	3. Assess		on		dewatering	
		excavation works	effectiveness		mitigation		processes;	
		or dewatering	of			4.	Consider	
	~	processes;	implemented		to be		changes	in
	5.	Discuss mitigation	mitigation		implement		working	1
		measures with	measures.	4	ed;			and
		IEC, Engineer and		4.	Assess	_	plans;	• . •
		Contractor;			effectivene			with
	6.	Ensure mitigation			ss of		,	and
		measures are			implement		U	and
	-	implemented.			ed		propose	
	7.	Increase the			mitigation		mitigation	4
		monitoring		~	measures;		measures	to
		frequency to daily		5.	Consider			and
		until no			and if		Engineer wit	
		exceedance of			necessary		three work	ung
		Limit level for two			instruct	6	days; Implement	
		consecutive days.			Contractor	0.	Implement	
					to slow		agreed	
					down or to		mitigation	

	stop all or part of the 7	measures; As directed by
	constructio	the Engineer,
	n activities until no	slow down or stop all or part
	exceedance	of the
	of Limit Level.	construction activities until
		no exceedance of Limit level.

5.7 Monitoring Schedule for the next reporting period

Hydrological characteristics monitoring schedule is proposed to be carried out on 2^{nd} , 9^{th} , 16^{th} , 23^{rd} and 30^{th} of May 2014.

6 Ecological Monitoring of ECA

6.1 Ecological Monitoring of ECA

6.1.1 Scope of Monitoring

The ECA was formally handed over to AFCD on 16th October 2012. The wire mesh fences and gate at the northwestern part of the ECA were fixed and reinstated by the Main Contractor. No site visit and ecological monitoring by the Wetland Specialist from the Main Contractor and the Ecologist from the IEC respectively were carried out in November 2012. The post-establishment phase monitoring and management of the ECA have commenced and to be undertaken by the AFCD in accordance with the monitoring and management items stipulated in the latest approved EM&A Manual of the Project

6.2 Monitoring Results

According to Table 6.17 of the EM&A Manual, ecological monitoring of the ECA will be carried out by qualified ecologists during the 1-year wetland establishment period of the ECA before handing over to AFCD for their post establishment monitoring. Establishment phase of the ECA began in September 2011, ecological monitoring programme was conducted and monitoring data was presented in respective monthly EM&A reports. Ecological monitoring programme ended in September 2012 and hence there will be no ECA report attached in EM&A reports.

6.2.1 Description of monitoring of transplanted Pavetta hongkongensis in Ecological Compensatory Area

According to the latest Transplantation Proposal, monitoring of the transplanted individual of *Pavetta hongkongensis* will cover a period of 12 months after the transplanting exercise. The monitoring will be conducted once a week in the first 3 months and once in each subsequent month in the remaining monitoring period. Health condition and growth of each transplanted individuals will be assessed and photographic records will be undertaken for each inspection.

6.2.2 Description of transplanted Pavetta hongkongensis and remarks

The monitoring of the transplanted individual of Pavetta hongkongensis has been covered a period of 12 months. Therefore, the monitoring for Pavetta hongkongensis was not carried out in this reporting period.

7 Landscape and Visual

7.1 Introduction

The Landscape and Visual Monitoring of the Project is conducted to fulfill Clauses 5.2 and 5.4 of EP-303/2008 and the monitoring requirements in accordance with Section 7 of the approved updated EM&A Manual (approved by EPD on 31st May 2012) of the Project. A Baseline Review on updating the landscape and visual condition, and the mitigation measures of the Project (including Contracts 1 and 2 of the Project) was undertaken before the commencement of the Project. The review findings were updated in the Baseline Environmental Monitoring Report submitted to the EPD on 14th February

2011.

This monthly monitoring report will detail the scope of landscape and visual monitoring work, monitoring findings and observations, and any recommendations and advice on proper implementation of the landscape mitigation measures in the works areas under Contract 1 of the Project.

7.2 Scope of Monitoring

7.2.1 Monitoring Objectives

Landscape and Visual Monitoring of the Project should be conducted in a bi-weekly basis for checking the design, implementation and maintenance of the landscape and visual mitigation measures throughout the construction phase and in a quarterly basis during operational phase of the Project. Observations of any potential conflicts between the proposed mitigation measures and the project works carried out by the Contractors should be recorded. Recommendation and advice on proper implementation of the landscape mitigation measures should be provided to the Contractor for minimizing any potential impacts on the landscape and visual elements.

7.2.2 Monitoring during Construction Phase

The following landscape and visual mitigation measure should be implemented during the construction phase of the project to minimize the potential impacts:

- Visual Screen Use of hoardings as visual screens for the construction in the works areas;
- Contaminant/ Sediment Control Use of temporary barriers, covers and drainage provision around the construction works as contaminant/ sediment control to prevent the contaminants and sediments from entering the sensitive water-based habitats;
- Pollution Control Implementation of pollution control measures to minimize any adverse environmental impacts to the surrounding habitats;
- Liaison with Nursery Liaison with the nursery operator as necessary to minimize any adverse impact to the daily operation and plant holding capacity of the nursery;
- Existing Trees within Works Area Maintenance and protection of the existing trees, especially their crowns, trunks and roots, within work sites; and
- Construction Light Provision of construction light should be controlled at night to avoid excessive glare to the surrounding villages and to Plover Cove.

7.2.3 Monitoring during Operational Phase

The following landscape and visual mitigation measure should be implemented during the operational phase of the project to minimize the potential impacts:

- Viewing area formation by planting with shrubs, grasses and benches along the area;
- Architectural design of the pump house will help it fit into the existing suburban, natural to semi-natural surroundings;
- Landscape design of pump house by providing sufficient planting around its boundary fence;
- Enhancement planting along Tung Tsz Road with shrubs/ trees of suitable species to help protect the stream and marshes;
- Construction of box culvert should be with at least 1.0m soil depth for enhancement planting;
- Transplanting of existing affected trees to adjacent locations should be carried out;
- Preparation for transplanting is needed to allow sufficient time for root pruning and rootball preparation prior to transplanting; and

• Reinstatement of affected area should be carried out to check that the works areas are properly reinstated.

7.3 Landscape and Visual Monitoring Results

7.3.1 Monitoring Date(s)

This monthly Landscape and Visual Monitoring (April 2014) was conducted to cover only Areas A, B and C of Contract 1 of the Project. The bi-weekly monitoring was conducted on 3rd, 15th and 28th April 2014.

Area C (i.e. Ecological Compensatory Area (ECA)) was formally handed over to AFCD on 16th October 2012 for management and maintenance. No access into the ECA is allowed after the handover.

All photos stated in this section are recorded in Appendix G.

The bi-weekly monitoring for Contract 2 was also undertaken on 3rd, 15th and 28th April 2014. The monitoring findings and recommendation will be submitted in a separate Monthly EM&A Report under Contract DC/2010/02.

7.3.2 Visual Screen

No follow-up action by the Contractor is required as from the *Monthly EM&A Report for March 2014*.

Observation

Temporary construction hoardings have been erected around Wai Ha River estuary since the building of an automatic mechanical penstock at the area (**Photo 1**). Since February 2014, the construction hoardings surrounding Area A (i.e. the proposed pump house station) have been replaced by the built boundary walls along the western and part of the northern sides of Area A (**Photo 2**), and chain-link fence erected along the rest of the boundary sides of Area A (**Photo 3**). Construction of the proposed roadside planters along Ting Kok Road has commenced in March 2014. The works areas were demarcated by temporary construction barriers (**Photo 4**).

The temporary hoardings established for demarcating the construction site boundary of Phases 1 and 2 construction works area of Area B in Tung Tsz Nursery have been removed since January 2014. The reinstatement works in the nursery have been under progress and the areas were partly demarcated with loosened barrier tapes (**Photos 5-6**). The open section and other reinstated access path connecting between Phases 1 and 2 works areas have been maintained during the current reinstatement work period, providing an access path for the daily operation of the nursery. Since November 2013, the hoarding along the eastern boundary of Phase 2 in Area B (i.e. the section next to Ting Kok Road) was permanently reinstated with the original chain-link fence. Canvas sheets were put on the reinstated fence to screen off the existing construction site from the pedestrian path (**Photo 7**).

The gate of the adjacent housing area near the previous main entrance of Area C has been reinstated at its original location by the Contractor since November 2012.

Recommendation

No specific recommendation is required.

7.3.3 Contaminant/ Sediment Control

No follow-up action by the Contractor is required as from the *Monthly EM&A Report for March 2014*.

Observation

Area A

The wheel washing facility at the entrance of Area A was removed as the major earthwork was completed and most of the ground surface in Area A has been turned into concrete road. According to the Main Contractor, no groundwater or used water was pumped from the excavated sites or built box culvert in April 2014.

Area B

The major excavation and construction works in Area B were completed, leaving minor excavation and reinstatement work for irrigation pipes and nursery beds in both Phases 1 and 2 within Tung Tsz Nursery. The wheel washing facility at the entrance of the access road leading towards the works area at northwestern part of Tung Tsz Nursery was removed. No reinstatement work was observed during the inspection on 15th and 28th April 2014, and no significant discharge of groundwater or used water from Area B was noted during the inspection in April 2014.

Area C

Area C was formally handed over to AFCD on 16th October 2012 for management and maintenance. The pond of the ECA has connected with the Wai Ha River directly. No water resulting from normal wetland maintenance practice was pumped out from the ECA.

Recommendation

The Contractor should regularly check the condition and locations of the drainage pipes and ensure that all used water should be appropriately filtered and discharged to the manholes/other discharge points agreed by the Engineer and EPD.

7.3.4 Pollution Control

All used water for construction works was filtered and drained to the manholes and drainage points, as following the recommendation stated in *Monthly EM&A Report for March 2014*.

Observation

Area A

The wheel washing facilities at the entrance of Area A was removed as the major earthwork was completed and most of the ground surface in Area A has been turned into concrete road. According to the Main Contractor, no groundwater or used water was pumped from the excavated sites or built box culvert during April 2014.

No direct discharge of water into the adjacent Wai Ha River was observed from the works area for building the automatic mechanical penstock at Wai Ha River estuary as no construction works were carried out as observed during the inspection in April 2014.

Area B

The major excavation and construction works in Area B were almost completed, leaving minor excavation and reinstatement work for irrigation pipes and nursery beds in both Phases 1 and 2 within Tung Tsz Nursery. The wheel washing facility at the entrance of the access road leading towards the works area at northwestern part of Tung Tsz Nursery was removed. No significant discharge of groundwater or used water from Area B was noted during the inspection in April 2014.

Area C

Area C was formally handed over to AFCD on 16th October 2012 for management and maintenance. The pond of the ECA has been connected to Wai Ha River directly as following the scheme design of Habitat Compensatory Plan. No direct discharge of turbid water into the adjacent Wai Ha River was observed through the fence of Tung Tsz Nursery (**Photo 8**).

Recommendation

The Contractor should regularly check the condition and locations of the drainage pipes and ensure that all used water should be appropriately filtered and discharged to the manholes/other discharge points agreed by the Engineer and EPD. This is to avoid any potential contamination to the vegetation in Shuen Wan marsh and other vegetated/marinated areas adjacent to the active works area.

7.3.5 Liaison with Nursery

Active construction works within Tung Tsz Nursery has been extended to the east of the nursery in connection with Ting Kok Road since May 2012. As mentioned above in Section 3.2.3, all temporary hoardings established for demarcating the construction site boundary in Tung Tsz Nursery have been removed in January 2014 and replaced by barrier tapes.

The works practice and maintenance of trees within the nursery generally follow the recommendation as stated in *Monthly EM&A Report for March 2014*. Any observed issues related to the liaison with the nursery are highlighted in this section.

Observation

The temporary hoardings were erected from northwest to southwest parts of Tung Tsz Nursery in Area B in April 2011, while those boundary hoardings around Phase 2 construction works were erected in May 2012. As mentioned above in Section 3.2.3, these temporary hoardings have been removed in January 2014, and the site boundary was subsequently demarcated with barrier tapes. In addition, the hoarding along the eastern boundary of Phase 2 in Area B was permanently reinstated with the original chain-link fence, which was further screened by canvas sheets (**Photo 7**).

No major excavation works were undertaken in Phases 1 and 2 in April 2014. The reinstatement works for the original access paths, ground of the nursery beds and basic nursery utility (such as irrigation pipes and lamp posts) were still in progress in both Phases 1 and 2 areas (**Photos 9-10**).

Regular monitoring for all transplanted and retained trees within the nursery was conducted on a bi-weekly basis. The dead, transplanted tree *Grevillea robusta* (U58) was already removed by the Contractor and its dry stump was left in the planter from October 2013. The entire planter of the removed tree was removed in February 2014.

As reported in the previous *Monthly EM&A Reports*, the retained tree U68 (*Gmelina arborea*) was found fallen after the severe typhoon in July 2012, with its leaning trunk

being pruned and removed in August 2012 (as reported in *Monthly EM&A Report for August 2012*). Regular removal of generated watersprouts was sometimes noted throughout the monitoring period. The entire planter was already removed in March 2014 and reported in the submitted *Monthly EM&A Report*.

Recommendation

The works area and the construction works should be properly managed and implemented without influencing the daily operation of the nursery (i.e. provide enough access paths and works area for the nursery operation).

All transplanted trees should be watered regularly (e.g. at least every two days during the dry season) by the appointed landscape contractor. Meanwhile, the Contractor should prevent forming waterlogged areas or leakage of used water from the active construction works area into the Nursery. This is to prevent causing any nuisance to the nursery's daily operation. In addition, the Contractor is recommended to replace or remove the broken bamboo stakes for the transplanted trees, as well as removal the climbers and weedy plants found in the tree canopies and planters of these transplanted trees prior to handing over the site back to the Nursery Operator.

The appointed landscape contractor and the Contractor should closely monitor the health conditions of all transplanted/relocated and retained trees throughout the construction period of the Project.

7.3.6 Existing Trees within Works Areas

Maintenance of the existing trees within the works areas generally follows the recommendations as stated in *Monthly EM&A Report for March 2014*, except that the surplus soil and tied strings on the trees have not yet removed and the broken planters have not yet repaired. The observations recorded in April 2014 are highlighted in the following sections.

Observation

Area A

Construction of the slanting component of the proposed green roof and pumping house was completed by end of January 2014. The proposed green roof on the pumping house was vegetated with herbaceous ground cover *Arachis duranensis* in accordance with the approved Landscape Plan. However, due to the severe weather and Black Rainstorm occurred and hoisted between 29th and 31st March 2014, the planting soil on the slanting component of the pumping house was washed out by the heavy rainstorm and the soil accumulated at the base of the planting house and the nearby planting area (**Photo 11**). The soil was removed subsequently as observed on 15th and 28th April 2014 (**Photo 12**). However, some planting soil was still found accumulated at the nearby planting area with the planted ground cover (*Iris tectorum*).

No significant damage caused by the severe weather was observed on the green roof of the pumping house (**Photo 13**), and other planted vegetation in Area A (such as *Ficus pumila* and *Parthenocissus dalzielii* on the ground for vertical greening, planted shrub *Ficus microcarpa* (Golden Leaf) and tree *Cinnamomum burmannii*) (**Photos 14-15**) in April 2014. However, some hydroseeded area may be affected as the sprayed grass seeds may be washed out by the heavy storm.

As observed in April 2014, the existing retained, relocated and compensatory trees in Area A were generally protected within the built planting areas or fenced outside the boundary fence (**Photo 16**). In addition, some sections of the newly established chain-link fence were cut to facilitate the growth of large scaffold branch of E44 (**Photo 17**).

The tree to be transplanted E16 (*Bombax ceiba*) was relocated to the southern side of Area A next to the site hoarding in July 2012. The tree was still in marginally fair condition in April 2014 (**Photo 18**) and it was separated outside the proposed chain-link fence along the boundary sides of Area A. Soil grade change was observed around the trunk base and minor exposed roots were found in January 2014. The stability of the tree may be affected. Though this tree is fenced outside the chain-link fence, the condition and stability of this tree should be regularly monitored.

The relocated tree E38 (*Melaleuca cajuputi* subsp. *cumingiana*) was found dead after its relocation in August 2013, and it was removed by the Contractor in November 2013 (reported in *Monthly EM&A Report for November 2013*). A planter was built at the same location in accordance with the approved Landscape Plan. The four newly planted *Cinnamomum burmannii* appeared in fair condition (**Photo 14**).

Two trees (*Melaleuca cajuputi* subsp. *cumingiana*) have been found in the northeastern part of Area A since February 2013 and they have remained in fair condition.

Damaged tree trunk on E55 (*Macaranga tanarius* var. *tomentosa*) has been reported in the submitted *Monthly EM&A Reports* since May 2013. The wound on the trunk of E55 has been burlapped since May 2013. The upper section of the tree trunk was broken in June 2013. The tree was still in very poor condition with most of its foliage as dry watersprouts only and it was separated outside the proposed chain-link fence along the boundary sides of Area A in March 2014 (**Photo 19**).

A retained tree T253 (*Bridelia tomentosa*) was in poor condition (**Photo 20**). Dead scaffold limbs with dry, peeled bark were observed. This identified tree defect may be only related to the intrinsic physiological and structural condition of T253. The tree was closely monitored in April 2014.

No other significant damages on the crowns, trunks and roots of the remaining trees resulting from the construction machinery were observed during the monitoring in April 2014 in Area A. A number of new trees (including one *Bridelia tomentosa*, two *Bombax ceiba*, eight *Macaranga tanarius* var. *tomentosa* and nine *Melaleuca cajuputi* subsp. *cumingiana*) have been planted along the eastern and southern parts, and at southwestern corner since January 2014. The two trees *Bombax ceiba* were replaced with new trees due to unsatisfactory condition. All these trees were tagged, and planted for compensation of the tree loss due to the influence of severe typhoons and poor tree condition.

Area B

As highlighted in the Section "Liaison with Nursery", the transplanted tree Grevillea

robusta (U58) was removed in October 2013 as it was certified as dead specimen. The entire planter of this removed tree was removed since February 2014.

The ground of Phases 1 and 2 areas were inundated by rainwater which was not yet drained as observed on 3rd April 2014. Except the relocated or retained trees protected on the planter, trunk bases of some of these trees were inundated by rainwater in early April 2014. The situation was reported to the Contractor immediately and the rainwater was drained subsequently.

The relocated tree U37 was certified as a dead specimen (**Photo 21**). Most of the excavated soil piled close to the relocated trees along both sides of Phase 1 works area was generally removed.

Half of the planter of U47 (*Terminalia catappa*) has been broken since August 2013, and some of its roots and planter soil were exposed in the air. As inspected in April 2014, the planter was still not yet repaired (**Photos 22-23**). The condition and stability of this tree was closely monitored. In addition to U47, the planters of U54 (*Terminalia catappa*) and another two untagged *Terminalia catappa* to the southeast of U54 (**Photos 24-26**), as well as the relocated tree U69 (*Alstonia scholaris*) were also broken and not yet repaired (**Photo 27**). Exposed roots and planter soil were observed. Leaning tree trunk was also observed on U69, probably due to the lack of intact planting soil to be supported within the broken planter. On the other hand, excavated soil was still piled around the planter and on the root flare of U51 (*Terminalia catappa*) (**Photo 28**).

U55 (*Pterocarpus indicus*) has been transplanted to its final receptor site in 2011 and pest control was applied on this tree in early 2013 due to the sign of termite infestation. Its health condition has been improved. The long branches with decayed wood and wounds were still observed in the canopy. Close monitoring on this tree is still required.

Sign of suspected termite infestation was observed at the lower trunk of the retained tree U67 (*Cassia fistula*). The tree was still in fair health and structural condition as observed in April 2014 (**Photo 29**), but close monitoring should be undertaken.

For the retained tree A40 (Terminalia catappa) at the entrance of Phase 2 construction

areas, the southern excavated area was refilled but the northern excavated area close to its planter has not yet backfilled with soil, and some of the tree roots growing underneath the tree planter are still under a risk of being damaged by any future minor civil works (**Photos 30-31**). The tree trunk was not guyed to the nearby tree planter as observed in April 2014. The tree may have a risk of leaning if its underground roots are further damaged or the ground is not backfilled soon.

The trunk of the transplanted tree U53 (*Terminalia catappa*) was still tied tightly by strings and a wrapping which was left after the transplantation of the tree (**Photo 32**). Wounds were found under the wrapping and watersprouts were observed developed on the trunk. As the strings were tied tightly on the trunk, they may girdle the tree and hence affect the tree health and its structure. Similar hessian wrapping and tied strings were also found on the relocated trees U57, A22, A42 and A41 (e.g. **Photo 33**).

Many relocated trees in Phases 1 and 2 works areas within the Nursery were in fairly poor to fair condition due to the poor transplantation skills and poor site condition. Proper tree protection (e.g. guying and temporary TPZ), removal of surplus soils (esp. those related to the reinstatement of irrigation system) and removal of climbers and weedy herbs in the planters of the relocated trees should be implemented as proper maintenance of the existing trees.

The remaining trees, including retained and transplanted specimens, within the nursery were maintained generally in fair condition, with no significant damage on tree crowns, trunks and roots observed during the monitoring in April 2014. Minor broken twigs were observed on some of these trees.

Area C

Area C was formally handed over to AFCD on 16th October 2012 for management and maintenance. The area was fenced off and no access was allowed.

Recommendations

Area A

Maintenance of proper TPZs covering the tree driplines with no temporarily stored construction materials, excessive stockpiled soil and waterlogged condition around the tree trunk flares were the major tree management issues in Areas A and B during the active construction period. Even only minor construction work and reinstatement work are left in this period, the Contractor is still advised to continue notifying the on-site workers not to stockpile soil/construction materials or place construction equipment within and close to the TPZs or lower trunks/trunk flares of retained/ relocated/ new trees. Any temporarily stored construction materials/ equipment and excessive water around the trunk flares should be removed or drained immediately. The Contractor should remind the operators of the construction machines and on-site workers to be aware of the presence of these relocated, retained or newly planted trees nearby their works (e.g. for the case of the retained trees in the eastern and southern parts of Area A), and prevent accidental damage on these trees as far as practical. Meanwhile, the Contractor and sub-contractor should carefully design the civil works. Common civil works, such as excavation and sheet piling works, should be programmed and designed carefully by taking tree buffer zone into consideration. The works should avoid affecting the tree canopy, trunk and underground root zone with regard to tree dripline as far as possible.

The Contractor is advised checking the condition of the orange construction nets in both Areas A and B, which have been used to demarcate the tree protection zone, and repair the damaged nets as soon as possible. The site workers should not remove the tree protection zone during the construction phase, and all site workers should be reminded to protect the existing/ relocated trees with appropriate tree protection measures.

The Contractor should continue the maintenance of proper tagging system for all trees within and outside the hoarded/fenced site in order to facilitate the monitoring of their existing condition. In addition, the Contractor should maintain regular monitoring of the tree protection system and condition of the retained and transplanted trees.

All retained trees or trees to be transplanted should be watered regularly (e.g. at least every two days) by the landscape contractor or on-site workers. The Contractor should conduct regular inspection on the health condition and protection measures of each existing trees within the Area A. In particular, regular watering should be applied on those relocated trees with regard to their poor health condition. If these trees or other transplanted/ relocated trees are found to be dead specimens in the wet season, the Contractor should replace these specimens. In addition, the appointed landscape construction should provide regular watering on all newly planted trees, shrubs, climbers and ground cover throughout the maintenance period.

The Contractor is advised to remove the soil which was washed away from the green roof during the period of severe rainstorm. The Contractor is also advised to implement soil erosion prevention measure on the slanting component of the pumping house so as to minimize the influence on the planted vegetation in the coming wet season.

Area B

All transplanted trees should be watered regularly (e.g. at least every two days during the dry season) by the landscape contractor. This is a necessary maintenance practice to improve the survival rates and growth for trees showing poor health condition as a result of the transplantation shock. Regular check of the tree health should be conducted. Proper protective measures such as guying and TPZs are recommended especially for the newly transplanted/ relocated trees. Waterlogged areas should be avoided and all used water/ temporary storage of construction materials or surplus soil around the tree trunk flares and close to the tree root zones should be drained out or removed immediately. To prevent accidental drainage of used water into the tree root zones of the relocated trees, the Contractor is recommended to establish a proper separation (e.g. sandbags barriers or wooden plates) between the trees and the ground of the active construction works. If in such circumstance that there is direct conflict between certain tree parts of the retained, transplanted or relocated tree(s) and the construction works/ machinery, the pruning works should be carried out in accordance with any local, national or international standards related to tree remedial works.

Regular inspection of the tree health of a number of trees (i.e. U47, U55, U67 and A40) should be undertaken to update their health condition and any deterioration of tree defects. The Contractor is advised checking the condition of all bamboo stakes used for staking transplanted trees, and replace any damaged stakes as soon as possible. If these trees or other transplanted/ relocated trees are found to be dead specimens in the wet season after

the assessment by the arborist of the appointed landscape contractor, the Contractor should replace these specimens. In addition, the Contractor should backfilled the excavated hole (such as that under A40) as soon as possible to prevent its further leaning due to the limited support from the ground. If practical, the Contractor is advised to replant any leaning trees, resulting from the less support of soil due to excavation works, back to upright position by end of the construction period.

The Contractor is recommended to remove all the wrapping and strings tied on the transplanted tree, especially for U53, U57, A22, A42 and A41, in order to prevent them from girdling the tree and influencing the tree health and structure.

The Contractor is advised repairing the broken planters of the trees U47, U54 and two nearby untagged *Terminalia catappa* and U69, and avoiding the stockpile of soil close to the trunk flare of U51.

All tree tags on the trees should be managed properly by the Contractor throughout the construction and establishment phases.

The Contractor is advised to programme the remaining minor civil works appropriately in Phases I and 2 of Area B. The Contractor should establish a buffer zone and tree protection zone between the civil works and the relocated/ retained trees wherever practical.

Area C

As Area C was handed over to AFCD for management and maintenance, no further recommendation is given.

7.3.7 Construction Lights

No follow-up action on maintenance of construction light is required as from the *Monthly EM&A Report for March 2014*.

Observation

No construction light impact to the surrounding villages and to Plover Cove as all construction activities and construction sites are halted at 1800. No construction light at night is provided by the Contractor.

Recommendation

No specific recommendation is required.

7.4 Audit Schedule

The next bi-weekly Landscape & Visual Monitoring in May 2014 is scheduled to be conducted in the weeks of 12th and 26th May 2014.

8 Action taken in Event of Exceedance

If the measurements (Noise, Water, Hydrological Characteristics, and Ecology) exceed the action / limit level, exceedance details will be reported and follow-up actions will be taken by relevant parties involved.

During the reporting month there was no exceedance for noise, hydrological characteristics, and ecological measurements recorded; therefore, no actions were taken.

There were 11 abnormal incidents of water quality limits (Turbidity) were recorded in this reporting month according to the established action and limit levels. ET has arranged site investigations for the abnormal incidents. No construction activities were carried out at the river bed. During the reporting period, construction of intake structure was conducted near Wai Ha River. Proper mitigation measures were implemented by contractor to avoid site water release to the Wai Ha river and no particular observation of defective site activities were found causing water contamination. The exceedances of Turbidity and SS were believed to be mainly attributed by adverse weather and natural fluctuation and adverse since the recorded levels of Turbidity and SS at control station had also exceeded its baseline action or limit level, the exceedances recorded at W2 were unlikely to be related to the Project.

The water condition of Wai Ha River is presented in photo attached in Appendix M.

9 Construction waste disposal

It is the contractor's responsibility to ensure that all wastes produced during the construction phase for the drainage improvement works are handled, stored and disposed of in accordance with good waste management practices and EPD's regulation and requirement. Waste materials generated during construction activities, such as construction and demolition (C&D) material, chemical wastes and general refuse, are recommended to be audited at regular intervals to ensure that proper storage, transportation and disposal practices are being implemented.

Table 9.1 is a summary of figures of the construction wastes disposal provided by Contractor.

	-		_								
	Ac	tual Quantities of	Inert C & D	Materials Gen	erated Month	nly	Actua	l Quantities of C	& D Waster	s Generated	Monthly
Month	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in'000m3)	(in'000m3)	(in'000m3)	(in'000m3)	(in'000m3)	(in'000m3)	(in'000kg)	(in'000kg)	(in'000kg)	(in'000kg)	(in'000kg)
Year2011	11.12	0.00	9.703	0.665	0.750	0.556	0.00	0.00	0.00	0.00	0.165
Year 2012	11.12	0.00	9.884	1.185	0.05	0.00	2.37	0.00	0.00	0.00	0.192
Jan 13	0.290	0.00	0.24	0.00	0.05	0.01	0.00	0.00	0.00	0.00	0.00
Feb 13	0.190	0.00	0.16	0.00	0.03	0.00	0.00	0.00	0.00	0.00	0.035
Mar 13	1.14	0.00	1.13	0.00	0.01	0.00	0.00	0.00	0.00	0.00	0.00
Apr 13	1.540	0.00	1.52	0.00	0.02	0.00	0.00	0.00	0.00	0.00	0.00
May 13	0.85	0.00	0.82	0.00	0.03	0.00	0.00	0.00	0.00	0.00	0.00
Jun 13	0.36	0.00	0.33	0.00	0.03	0.00	0.00	0.00	0.00	0.00	0.00
Jul 13	0.255	0.00	0.24	0.00	0.015	0.00	0.00	0.00	0.00	0.00	0.00
Aug 13	0.08	0.00	0.08	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Sep 13	0.04	0.00	0.04	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.02
Oct 13	0.04	0.00	0.04	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.02
Nov-13	0.04	0.00	0.04	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Dec-13	0.04	0.00	0.04	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.02
Jan-14	0.06	0.00	0.06	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.01
Feb-14	0.00	0.00	0.0.0	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Mar-14	0.00	0.00	0.0.0	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Apr-14	0.00	0.00	0.0.0	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total	27.162	0.00	24.327	1.85	0.985	0.566	2.37	0.00	0.00	0.00	0.48
		Fo	recast of Tota	al Quantities o	f C & D Mat	erials to be C	Generated fi	rom the Contract			
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Wittais	Paper/cardboard packaging	Plastics (see note3)	Chemical Waste	Others, e.g. general refuse
	(in'000m3)	(in'000m3)	(in'000m3)	(in'000m3)		(in'000m3)			(in'000kg)		(in'000kg)
	0.04	0	0.04	0.0	0.00	0.00	0	0.01	0.00	0.1	0.02

Table 9.1 Summary of Construction Waste Disposal

Notes (1) The Performance targets are given in PS Clause 26.23 (14)

(2) The waste flow table shall also include C & D materials that are specified in the Contract to be imported for used at the sites

(3) Plastics refer to plastics bottles/containers, plastic sheets/foam from packaging materials.

Contract No. DC/2009/22 – Drainage Improvement in Shuen Wan, Tai Po – Contract 1 Monthly EM&A Report for April 2014

⁽⁴⁾ The summary table shall be submitted to the Engineer's Representative monthly together with the Waste Flow Table for review and monitoring in accordance with the PS Clause 25.20A(4)

10 Status of Permits and Licenses obtained

Table 10.1 is the updated status of environmental related permits/ license obtained for the construction activities.

Description	License / Permit No.#	Date of Issue	Site	Date of expiry	Status
Environmental Permit	EP-303/2008	2008/2/25	Area A, B & C	not applicable	Valid
Discharge License	WT00006448-2010	2010/6/15	Area A, B & C	30/6/2015	Valid
Registration as a Chemical Waste Producer	316597	2010/4/26	Area A, B & C	not applicable	Valid
Waste Disposal	7010348	2010/3/2	Area A, B & C	not applicable	Valid

Table 10.1 Status of Permits and Licenses Obtained

11 Compliant Log

There was no formal complaint received during the reporting period. Therefore, follow up actions for the environmental complaint is not required.

	Noise	Water	Ecology	Others
Year 2011	0	0	0	0
Year 2012	0	0	0	0
Year 2013	0	0	0	0
January 2014	0	0	0	0
February 2014	0	0	0	0
March 2014	0	0	0	0
April 2014	0	0	0	0
Total	0	0	0	0

Table 11.1 Summary of Formal Complaints received

12 Site Environmental Audits

12.1 Site Inspection

Site inspections were undertaken weekly to inspect the construction activities in active site areas to ensure that appropriate environmental protection and pollution control mitigation measures are properly implemented.

Within this reporting period, site inspections were conducted on 2nd, 11th, 17st and 25th of April 2014. A detailed checklist of each site inspection together with comments and relevant photos have been filed and kept. The findings from inspection were summarized in Table 12.1.

Date	Findings	Identification	Advice from ET	Action taken	Closing date
N/A	No major environmental deficiencies were observed during this	N/A	N/A	N/A	N/A

Table 12.1 Summary results of site inspections findings

Date	Findings	Identification	Advice from ET	Action taken	Closing date
	reporting				
	period.				

12.2 Compliance with legal and Contractual requirement

There was no non-compliance recorded for the month of April 2014.

12.3 Implementation status and effectiveness of the mitigation measures

Contractor has implemented mitigation measures to address those problems as advised by ER and ET. Some of the measures taken by the contractor were considered as effective to minimize negative impact to the environment. Ongoing investigation will be carried out to observe performance and effectiveness of those measures. Outstanding environmental items will be inspected in next month.

As there were some ongoing follow up practices, contractor was reminded to regularly review and rectify the discrepancy once found and maintain good site condition. The contractor implemented various environmental mitigation measures as recommended in the Environmental Permit and Final Mitigation Measures Report.

The recommend mitigation measures of EM&A manual (revision 3) are presented in **Appendix H** (A).

The implemented statues of mitigation measures are presented in **Appendix H (B)**

13 Future Key issues and recommendations

According to the forecasted site activities, key environmental issued to be considered should at least include:

- Site water control and relevant protective measures.
- Quality of effluent discharge from Area A.
- Control and disposal for construction wastes generated from works.

- Routine water spraying for dust control.

Tree protective measure for tree planting and transplanting, should be implemented, such as tree protection zone and regular watering.

14 Conclusions

Rectification works at Ting Kok Road, remaining works at intake structure and reinstatement in Tung Tzs Nursery were major site activities being carried out within this reporting period.

Regular site meetings and inspection audits led by the seniors for discussing site environmental matters were held among Project Proponent, Contractor and the ET on weekly basis. Also monthly site meeting and inspection audits with the above parties and IEC were carried out on 25th of April 2014.

For noise level monitoring, all results were within the established A/L limits.


For water quality monitoring, total 11 abnormal incidents of water quality criteria were recorded in this reporting month. During the reporting period, no construction activities were conducted near the Wai Ha River. Proper mitigation measures were implemented by contractor to avoid site water releasing to the Wai Ha river and no particular observation of defective site activities were found causing water contamination. The exceedances of Turbidity and SS were believed to be mainly attributed by natural fluctuation and adverse weather And, since the recorded levels of Turbidity and SS at control station had also exceeded its baseline action or limit level, the exceedances recorded at W2 were unlikely to be related to the Project.

Also, there were not any notifications of summons recorded during the reporting period. Furthermore, there were not any formal prosecution and complaints recorded.


ET has reminded the contractor to provide environmental pollution control measures wherever necessary, and to keep a good environmental management at site practice.

The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual (revision 3) and Environmental Permit requirement.

Appendix A: Site Location Plan

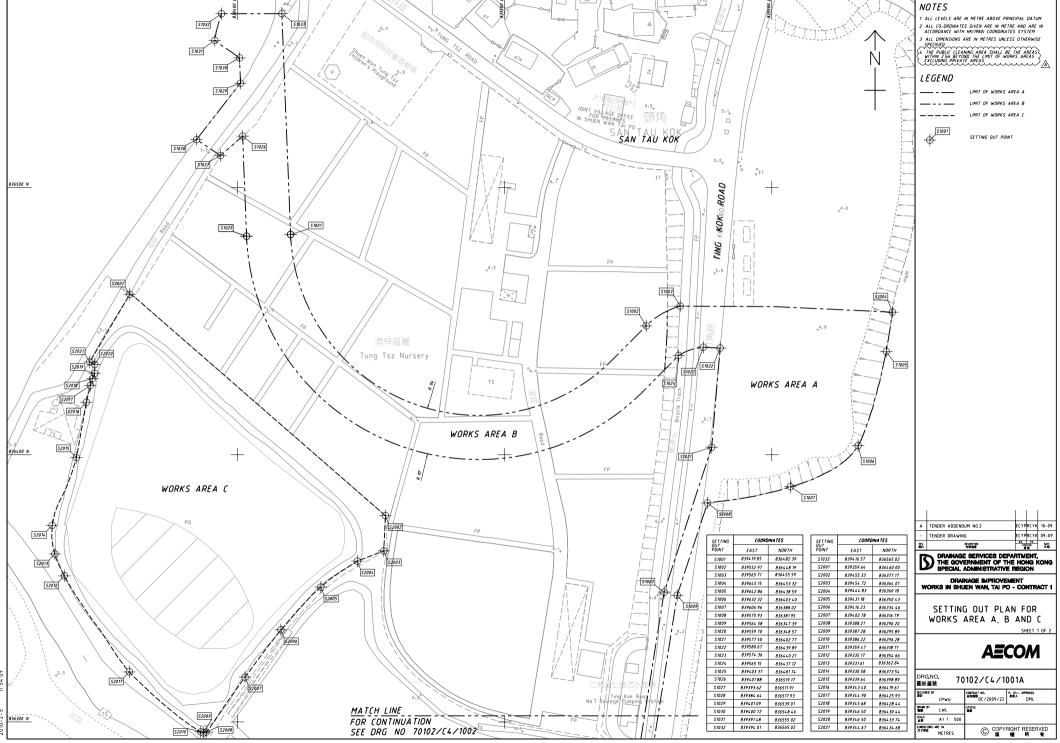

p:\projects\70102\1000\TENDER_ADDENDUM_NO_2\1001A.dgn

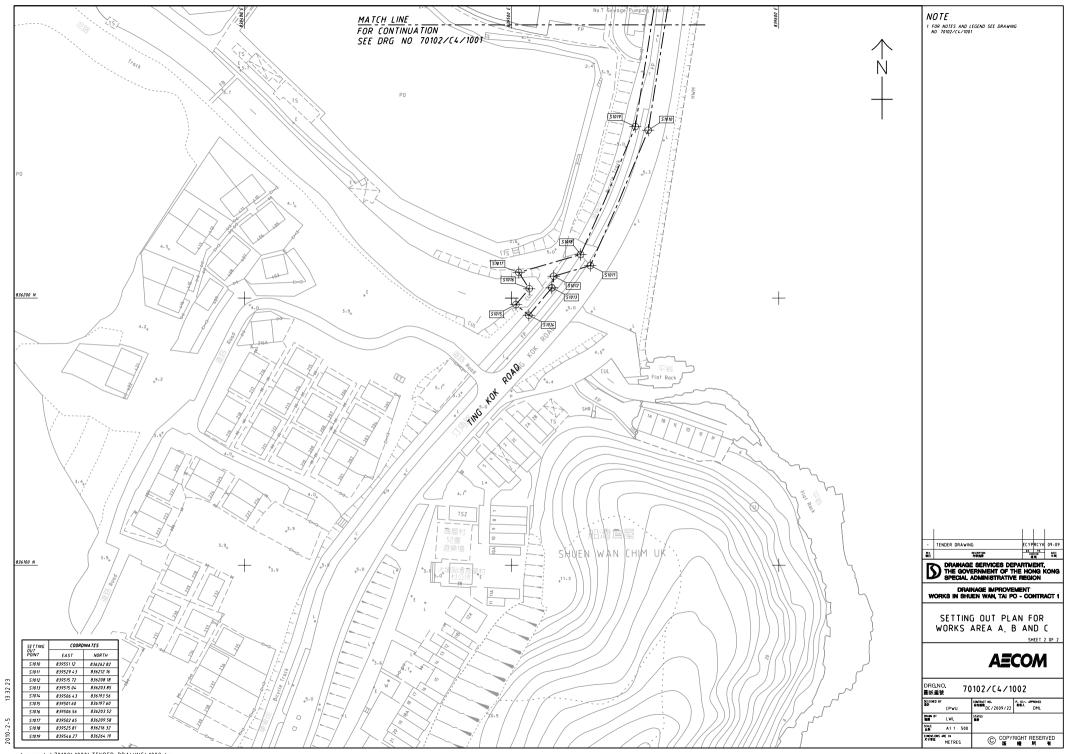

p:\projects\70102\1000\TENDER_DRAWING\1002.dgn

Appendix B: Key Personal Contact information chart

Post	Name	Contact No.	Contact Fax	e-mail
Project Manager	Mr. W. K. Chan	6821 1136	2674 6688	dc200922jv_pmcwk @yahoo.com.hk
Site Agent	Mr. K. M. Ma	9552 1734	2674 6688	dc200922jv_suba@ya hoo.com.hk
Environmental Officer	Mr. W. K. Chan	N/A	2674 6688	dc200922jv_pmcwk @yahoo.com.hk
Environmental Supervisor	Mr. Anthony Chan	9179 2092	2674 6688	anthony277@hotmail. com
Asia Ecological Consultants Ltd. (Wetland Specialist)	Dr. Mike Leven	2486 2885	2471 8389	mrleven@asiaecol.co m.hk
Environmental Pioneers & Solutions Limited (Environmental Team)	Mr. Johnny Lee	2889 0569	2856 2010	johnnylee@epsl.com. hk

Appendix C: Calibration Certificates for Measuring Instruments



FACTORY CALIBRATION DATA OF THE SVAN971 No. 34348

with preamplifier SVANTEK type SV18 No. 32160 and with microphone ACO type 7052E No. 54654

1. CALIBRATION (acoustical)

LEVEL METER function; Range: Low; Reference frequency: 1000Hz; Sound Pressure Level: 113.94 dB.

Characteristic	Correct value [dB]	Indication [dB]	Error (dB)
Z	113.94	113.95	0.01
A	113.94	113.95	0.01
C	[13.94	113.95	0.01

Calibration measured with the microphone ACO type 7052E No. 54654. Calibration factor: 0.50 dB.

3. LINEARITY TEST (electrical)

LEVEL METER function; Range: Low; Characteristic: A; f an = 31.5 Hz											
Nominal result LEQ [dB]	24.0	25.0	26.0	28.0	30,0	40.0	60.0	83.0			
Error dB	0.1	0.1	0,0	0.0	0,0	0.0	U.0	0.0			

LEVEL METER function; Range: Low; Characteristic: A; fim=1000 Hz

Nominal result LEQ [dB]	24.0	25.0	26.0	28.0	30.0	40,0	60.0	80.0	100.0	123.0
Error (dB)	0.0	+0.0	0.0	-0.0	+0.0	-0.0	-0,0	-0.0	-0,0	-0.0

LEVEL METER function; Range: Low; Characteristic: A: f ===== 8000 Hz

Nominal result LEQ [dB]	24.0	25.0	26.0	28,0	30.0	40,0	60.0	89.0	100.0	122.0
Error (dB)	0.0	-0.0	-0.0	-0.0	-0,1	+0,1	-0.0	-0,0	-0.0	-0.0

LEVEL METER function: Range: High; Characteristic: A: f == 31.5 Hz

	-							
Nominal result LEQ [dB]	34.0	35.0	36.0	38.0	40,0	60.0	80,0	97.0
Error dB	0,0	0.0	0.0	0,0	0,0	0.0	-0.0	0,0

LEVEL METER function: Range: High; Characteristic: A; f an= 1000 Hz

Nominal result LEQ [dB]	34,0	35.0	36.0	38.0	40.0	60.0	80.0	100,0	120,0	137.0
Error (dB)	0.0	-0.0	-0.0	0,0	-0.0	-0,0	-0.0	-0,0	•0.0	-0,0

LEVEL METER function; Range: High; Characteristic: A: f an= 8000 Hz

Nominal result LEQ [dB]	34.0	35.0	36.0	38.0	40.0	60.0	80,0	100.0	120.0	136.0
Error (dB)	-0,0	-0.0	-0.0	-0,0	-0.1	-0.0	-0.0	-0.0	-0,0	+0.0

1/3 OCTAVE (1kHz); Range: Low; f em= 1000 Hz

Nominal result [dB]	25.0	30.0	40,0	60.0	80,0	100.0	120,0	123.0	L
Error [dB]	-0,0	-0.0	+0.0	-0,0	-0.0	+0,0	-0.0	+0.0	L

4. TONE BURST RESPONSE

LEVEL METER function: Characteristic: A: f an= 4000 Hz: Burst duration: 2s

Range: Low; Steady level nominal result = 120dB

Result	Detector	Duration [ms]	1000	500	200	100	50	20	10	5	2	ī	0.5	0.25
	Fast	Indication [dB]	120.0	119.9	119.0	117.4	115.2	111.7	108.8	105.9	102.0	98.9	95.9	92.9
MAX	- ast	Error (dB)	0,0	0,D	0.0	0.0	-0.0	-0.0	-0.1	0.0	-0.0	-0.0	-0.1	-0.1
main	Slow	Indication [dB]	117.9	115.9	112.5	109.7	106.8	102.8	99.9	96.9	92.9	•		
	51011	Error (dB)	-0.0	-0.0	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	•0.1	•	-	
SEL		Indication (dB	120.0	117.0	113.0	110.0	107.0	103.0	100.0	97.0	93.0	89.9	86.9	83.9
JEL	•	Error (dB)	0.0	-0.0	0.0	0.0	-0.0	0.0	0.0	-0.0	-0.0	-0.0	-0.1	-01

*** SUAN971 No. 34348 page 1 ***

Range: Low: Steady level nominal result = 60dB

- 1	Result	Di												
1	Result	Detector	Duration msj	1600	500	200	100	50	20	10	5	2		0.5
		Fast	Indication [dB]	69.0	59.9	59.0	57.4	55.2	51.7	48 8	45.9	42.0	38.9	35.9
j	MAX		Error dB	0.0	0.0	0.0	0.0	-0.0	-0.0	-0.0	0.0	-0.0	-4.1	-0.1
1		Slow	Indication [dB]	57.9	55.9	52.5	49.7	46.8	42.9	39.9	36.9	32.9		
	·	3.0%	Error (dB)	-0.1	-0.0	-0.1	-0.1	-0.1	-0.1	-0.1	-0.1	-0,1		⊢:́─
	SEL	i .	Indication [dB]	60.0	57.0	53.0	50.0	47.0	43.0	40.D	37.0	33.0	30.0	27,0
į			Error (dB)	0.0	-0.0	0.0	0.0	-0.0	0.0	0.0	-0.0	0.0	-0.0	-0.0

Range: Low; Steady level nominal result = 35dB

Result	Detector	Duration [ms]	1000	500	200
	Fast	Indication [dB]	35.0	34.9	34,0
MAX	T ast	Error (dB)	0.0	-0.0	0.1
MAA	Slow	Indication dB	32.9	30.9	27.6
	5104	Error (dB)	-0.0	-0.0	-0.D
SEL	_	Indication [dB]	35.0	32.0	28.1
02.0		Error dB	0.0	-0.0	0.1

Range: High: Steady level nominal result = 134dB

Result	Detector	Duration [ms]	1000	500	200	100	50	20	10	ŝ		<u> </u>	0.5	0.25
	Fast	Indication (dB	134,0	133.9	133.0	131.4	129.2	125.7	122.8	119.9	116.0	112.9	109.9	106.9
MAX	Fast	Error dB	-0.0	0.0	0.0	0.0	-0.0	-0.0	-0.1	0.0	-0.0	-0.1	-0.1	U.I
	Slow	Indication [dB]	131.9	129.8	126.5	123.7	120.8	116.8	113.9	110.9	106.9	-		
L		Error [dB]	-0.1	-0.0	-0.1	-0,1	-0.1	-0.2	-0.1	-0.1	-0.1		<u> </u>	<u> </u>
SEL	-	Indication dB	134.0	131.0	127.0	124.0	121.0	117.0	114.0	111.0	107.0	103.9	100.9	97.9
L		Error dB	-0.0	-0.0	a.a	-0.9	-0.0	0.0	-0.0	-0.0	-0.0	-0.1	-0.1	-0.1

Range: High: Steady level nominal result = 54dB

Result	Detector	Duration [ms]	1000	500	200	100	50
	Fast	Indication [dB]	54.0	53.9	51.0	31.4	49.1
MAX	Fast	Error [dB]	-0.0	0.0	0.0	-0.0	-0.0
1970	Slow	Indication (dB)	51.9	49.B	46.5	43.7	40.8
	3100	Error [dB]	-0.1	-0.6	-0.1	-0.1	-0.1
SEL		Indication [dB]	54.0	51.0	47.0	44.0	41.0
JLC	•	Error [dB]	-0.0	-41.0	0.0	0.0	0.0

Range: High: Steady level nominal result = 46dB

Result	Detector	Duration [ms]	1000	500	200
	Fast	Indication [dB]	46,0	45.9	45.0
MAX	Fast	Error (dB)	0.0	-0.0	0.0
MAA	Slow	Indication [dB]	43.9	41.8	38.5
	310%	Error (dB)	-0.0	-0.0	-0,1
SEL		Indication [dB]	46.0	43.0	39.0
010		Error [dB]	0.0	-0.0	0.1

5. FREQUENCY RESPONSE' (electrical)

LEVEL METER function: Characteristic: Z; Range: Low: Input signal =120 dB;

	Colculated Filter Response	
0.25		
6 a	19.0 (0.9 d) 100000 (0.000000)	

Mea	sured i			c with I A-atten		lifier SVI 2.
	-T Hz	9 [9B]	Î[Hz]	A [dB]	f Hz	A [d8]
	10	0.1	6.3	-0.0	400J	0.0
	12.5	0.0	125	0.0	8000	0.0
	16	-0.0	250	0,0	16000	0.0
	20	-0.0	500	0.0	20000	0.0
	25	-0.0	1000	0.0		
	31.5	-0.0	2000	0.0	_	

All frequencies are nominal center values for the 3/3 octave bands

6. INTERNAL NOISE LEVEL[®] (electrical - compensated)

Characteristic	Z	A	C
Level [dB]	≤20	≤12	≤12

measured with preamplifier SVANTEK type SVI8 No. 32160.

7. INTERNAL NOISE LEVEL (acoustical - compensated)

LEVEL METER function:	Characteristic: A; (E	Backlight – off)

Range	Low	High
Indication [dB]	≤15	20.4

Noise measured in special chamber, with reference microphone G.R.A.S type 40AN No. 73421

ENVIRONMENTAL CONDITIONS

Temperature	Relative humidity	Ambient pressure
26 °C	31%	992 hPa

TEST EQUIPMENT

Item	Manufacturer	Model	Serial no.	Description
1.	SVANTEK	SVAN 401	65	Signal generator
2.	SVANTEK	SVAN 912A	4369	Sound & Vibration Analyser
3.	KEITHLEY	2000	0910165	Digital multimeter
4.	SVANTĖK	SV30A	7449	Acoustic calibrator
5.	SVANTEK	ST02	-	Microphone equivalent electrical impedance (18nF)

CONFORMITY & TEST DECLARATION

1. Herewith Svantek company declares that this instrument has been calibrated and tested in compliance with the internal ISO9601 procedures and meets all specification given in the Manual(s) or respectively surpass them.

2. The acoustic calibration was performed using the Sound Calibrator and is traceable to the GUM (Central Office of Measures) reference standard - sound level calibrator type 4231 No 2292773.

3. The vibrational calibration was performed using the Back to-Back Comparison method and is traceable to the GUM (Central Office of Measures) reference standard - accelerometer type 8305 No 1435233.

4. The information appearing on this sheet has been compiled specifically for this instrument. This form is produced with advanced equipment & procedures which permit comprehensive quality assurance verification of all data supplied herein.

5. This calibration sheet shall not be reproduced except in full, without written permission of the SVANTEK Ltd.

Calibration specialist: Ryszard Leoniak

Test date: 2013-05-22



ALS Technichem (HK) Pty Ltd 11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street Kwai Chung, N.T., Hong Kong T: +852 2610 1044 F: +852 2610 2021 www.alsglobal.com

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR ALLEN CHAN CLIENT: ENVIRONMENTAL PIONEERS & SOLUTIONS LIMITED ADDRESS: FLAT A, 19/F, CHAI WAN INDUSTRIAL BUILDING, 20 LEE CHUNG STREET, CHAI WAN, HONG KONG
 WORK ORDER:
 HK1402962

 LABORATORY:
 HONG KONG

 DATE RECEIVED:
 28/01/2014

 DATE OF ISSUE:
 07/02/2014

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory. Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal aceptance criteria of ALS will be followed.

Scope of Test:	Conductivity, Dissolved Oxygen, pH, Temperature and Turbidity
Equipment Type:	Multimeter
Brand Name:	Horiba
Model No.:	U-54-2 Multiparameter Probe
Serial No.:	T825CR6N
Equipment No.:	
Date of Calibration:	06 February, 2014

NOTES

This is the Final Report and supersedes any preliminary report with this batch number. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Fung Lim Chee, Richard General Manager -

General Manager -Greater China & Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order: Date of Issue: Client:	HK1402962 07/02/2014 ENVIRONMENTAL PIONEERS &	& SOLUTIONS LIMITED	A	
Description: Brand Name: Model No.: Serial No.: Equipment No.: Date of Calibration:	Multimeter Horiba U-54-2 Multiparameter Probe T825CR6N 06 February, 2014 Date of next Calibration: 06 May, 2014			
Parameters:				
Conductivity	Method Ref: APHA (21st edition Expected Reading (uS/cm)	on), 2510B Displayed Reading (uS/cm)	Tolerance (%)	
	146.9 6667 12890 58670	136.6 6800 13000 61500	-7.0 2.0 0.9 4.8	
Tolerance Limit (±%) 10.0 Dissolved Oxygen Method Ref: APHA (21st edition), 45000: G				
	Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)	
	3.66 5.72 8.89	3.58 5.76 8.81	-0.08 0.04 -0.08	
		Tolerance Limit (±mg/L)	0.20	

pH Value

Method Ref: APHA 21st Ed. 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	3.86	-0.14
7.0 10.0	7.17 10.10	0.17 0.10
	Tolerance Limit (±pH unit)	0.20

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Proc

ide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.				
Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)		
12.0	11.44	-0.6		
23.0	23.11	0.1		
35.0	34.99	0.0		
V SPOLAL LAND	10 1-1-1-2010-03-011			
Tolerance Limit (±°C) 2.0				

Turbidity

Method Ref: APHA (21st edition), 2130B

Method Ref. AFHA (21st edition), 2150B				
Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)		
0	0.0			
4	4.3	7.5		
40	38.7	-3.2		
80	82.2	2.8		
400	402	0.5		
800	812	1.5		
	Tolerance Limit (±%)	10.0		

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

, Mr. Fung Lim Chee, Richard General Manager -Greater China & Hong Kong

ALS Technichem (HK) Pty Ltd



Calibration Certificate

Certificate No.	38909		Page	1 of 2	Pages
Customer :	Environmental Pioneers and Solu	tions Limited			
Address :	Flat A, 19/F., Chai Wan Industria	Centre Building, 20) Lee Chung Stre	eet, Chai Wan	, НК .
Order No. :	Q33517		Date of receipt	:	6-Dec-13
Item Tested					
Description :	Protable Level-Velocity Logger				
Manufacturer :	•				
Model :	Stingray		Serial No.	: 45525	
Test Conditie	ons				
Date of Test :	2-Jan-14		Supply Voltage	:	
Ambient Temp	erature : (23 ± 3)°C		Relative Humid	lity:(50 ± 25) %
Test Specific	cations				
Calibration chec	k.				
Ref. Document/	Procedure: V12, T03, M07.				
Test Results				=	
All results were	within the tolerance(s).				
	shown in the attached page(s).				
Main Test equip	ment used:				
Equipment No.	Description	Cert. No.		Traceable to	
S179	Std. Tape	35142		NIM-PRC	
S136A	Stop Watch	37007		SCL-HKSAR	
S214A	Std. Thermo-Hygrometer	35472		SCS-SWISS	, NIM-PRC
will not include allow overloading, mis-ha	this Calibration Certificate only relate to t vance for the equipment long term drift, va indling, or the capability of any other labor age resulting from the use of the equipme	ariations with environme ratory to repeat the meas	ntal changes, vibratio	on and shock du	ing transportation,
	used for calibration are traceable to Inter bly to the above Unit-Under-Test only	national System of Units	s (SI).		
Calibrated by	:N Ү. К. Wong	Арр	roved by :	Alan Chu	
This Certificate is issued I	by:	Date	2-Jan-14		

Hong Kong Calibration Ltd. Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong. Tel: 2425 8601 Fax: 2425 8646



Calibration Certificate

Certificate No. 38909

Page 2 of 2 Pages

Results :

1. Flow Rate

Applied Value (Ft/s)	UUT Reading (Ft/s)	Tolerance	Uncertainty
2.06	2.0	± 5 % f.s	±1%

2. Level

Applied Value (Ft)	UUT Reading (Ft)	Tolerance	Uncertainty
1.00	1.0	± 5 % f.s.	± 0.1 %
2.00	2.0		
3.00	3.0		
4.00	4.0		

3. Temperature

Applied Value (℃)	UUT Reading (°C)	Tolerance	Uncertainty
22.5	22	± 2 °C	± 0.2 ℃

Remarks : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Sensor Used : Model : QZ02L-UT-01-PS

S/N:10D18289

----- END -----

Appendix D: Construction Noise Monitoring Data

Noise Monitoring Data Sheet

Monitoring Location		M1	AL1
Monitoring Method		Façade	Façade
Date of Monitorir	ng	2/4/2014	2/4/2014
Weather Condition	on	Cloudy	Cloudy
Measurement St	art Time (hh:mm)	9:25	10:05
Measurement Ti	me Length (mins)	30 r	nins
SLM Model & S/	N	SVAI	N 955
Wind Speed (m/s	s)	0.2	0.2
	L _{eq} (dB(A))	64.5	69.7
Measurement Results	L ₁₀ (dB(A))	66.7	71.2
rtoouno	L ₉₀ (dB(A))	50.4	60.4
Major Construction Noise Source(s) During Monitoring		The measured noise level was dominated by the background noise in the immediate vicinity of the monitoring location due to its large distance from the construction activities	The measured noise level was dominated by the background noise in the immediate vicinity of the monitoring location due to its large distance from the construction activities
Other Noise Source(s) During Monitoring		– Background Noise – Traffic Noise	– Background Noise – Traffic Noise

 Name
 Signature
 Date

 Perpared by:
 Lau Kai Chung
 Lau Kai Chung
 2/4/2014

Noise Monitoring Data Sheet

Monitoring Location		M1	AL1
Monitoring Method		Façade	Façade
Date of Monitorir	ng	9/4/2014	9/4/2014
Weather Conditi	on	Sunny	Sunny
Measurement St	art Time (hh:mm)	9:50	10:45
Measurement Ti	me Length (mins)	30 r	nins
SLM Model & S/	N	SVA	N 955
Wind Speed (m/	s)	0.2	0.2
	L _{eq} (dB(A))	63.3	68.8
Measurement Results	L ₁₀ (dB(A))	65.7	70.1
rtoouno	L ₉₀ (dB(A))	47.1	58.9
Major Construction Noise Source(s) During Monitoring		The measured noise level was dominated by the background noise in the immediate vicinity of the monitoring location due to its large distance from the construction activities	The measured noise level was dominated by the background noise in the immediate vicinity of the monitoring location due to its large distance from the construction activities
Other Noise Source(s) During Monitoring		– Background Noise – Traffic Noise	– Background Noise – Traffic Noise

Perpared by:

<u>Lau Kai Chung</u>

Name

<u>Lau Kai Chung</u>

Signature

9/4/2014

Date

Noise Monitoring Data Sheet

Monitoring Location		M1	AL1
Monitoring Method		Façade	Façade
Date of Monitorin	g	16/4/2014	16/4/2014
Weather Condition	on	Sunny	Sunny
Measurement Sta	art Time (hh:mm)	9:30	10:05
Measurement Tir	me Length (mins)	30 r	nins
SLM Model & S/I	N	SVA	N 955
Wind Speed (m/s	5)	0.2	0.2
	L _{eq} (dB(A))	62.5	66.7
Measurement Results	L ₁₀ (dB(A))	63.8	67.8
	L ₉₀ (dB(A))	49.7	53.5
Major Construction Noise Source(s) During Monitoring		The measured noise level was dominated by the background noise in the immediate vicinity of the monitoring location due to its large distance from the construction activities	The measured noise level was dominated by the background noise in the immediate vicinity of the monitoring location due to its large distance from the construction activities
Other Noise Source(s) During Monitoring		– Background Noise – Traffic Noise	– Background Noise – Traffic Noise

Perpared by:

<u>Lau Kai Chung</u>

Name

<u>Lau Kai Chung</u>

Signature

16/4/2014

<u>Date</u>

Noise Monitoring Data Sheet

Monitoring Location		M1	AL1
Monitoring Method		Façade	Façade
Date of Monitorin	g	23/4/2014	23/4/2014
Weather Condition	on	Cloudy	Cloudy
Measurement Sta	art Time (hh:mm)	14:00	14:40
Measurement Tir	me Length (mins)	30 r	nins
SLM Model & S/I	N	SVAI	N 955
Wind Speed (m/s	5)	0.2	0.2
	L _{eq} (dB(A))	62.3	67.8
Measurement Results	L ₁₀ (dB(A))	64.7	70.3
	L ₉₀ (dB(A))	49.9	54.1
Major Construction Noise Source(s) During Monitoring		The measured noise level was dominated by the background noise in the immediate vicinity of the monitoring location due to its large distance from the construction activities	The measured noise level was dominated by the background noise in the immediate vicinity of the monitoring location due to its large distance from the construction activities
Other Noise Source(s) During Monitoring		– Background Noise – Traffic Noise	– Background Noise – Traffic Noise

Perpared by:

<u>Lau Kai Chung</u>

Name

Lau Kai Chung

Signature

23/4/2014

Date

Noise Monitoring Data Sheet

Monitoring Location		M1	AL1
Monitoring Method		Façade	Façade
Date of Monitorin	g	30/4/2014	30/4/2014
Weather Condition	n	Sunny	Sunny
Measurement Sta	art Time (hh:mm)	14:30	15:05
Measurement Tir	ne Length (mins)	30 r	nins
SLM Model & S/N	N	SVA	N 955
Wind Speed (m/s	s)	0.2	0.2
	L _{eq} (dB(A))	64.5	68.7
Measurement Results	L ₁₀ (dB(A))	67.1	70.9
rtoodito	L ₉₀ (dB(A))	53.4	58.1
Major Construction Noise Source(s) During Monitoring		The measured noise level was dominated by the background noise in the immediate vicinity of the monitoring location due to its large distance from the construction activities	The measured noise level was dominated by the background noise in the immediate vicinity of the monitoring location due to its large distance from the construction activities
Other Noise Source(s) During Monitoring		– Background Noise – Traffic Noise	– Background Noise – Traffic Noise

Perpared by:

<u>Lau Kai Chung</u>

Name

Lau Kai Chung

Signature

30/4/2014

<u>Date</u>

Appendix E: Water Quality Monitoring Data

Remark:

Red highlighting: The value is exceeding limit level

Yellow highlighting: The value is exceeding action levele

Date of Sampling : 2/4/2014

Weather: Cloudy

Monitoring Location	W1	W2	C2
Time (hhmm)	14:12	15:40	14:45
Tide Mode	Mid	-ebb	N/A
Water Depth (m)	<1	<1	<1
pH value	6.70	7.78	6.40
Temperature (°C)	20.5	18.3	22
Turbidity (NTU)	4.30	41.4	3.20
DO (mg/L)	7.30	8.15	8.10
DO Saturation (%)	81%	90%	89%
Suspended Solids (mg/L)	8.0	23.0	4.0

Date of Sampling : 4/4/2014

Weather: Cloudy

Monitoring Location	W1	W2	C2
Time (hhmm)	16:02	16:00	16:24
Tide Mode	Mid	-ebb	N/A
Water Depth (m)	<1	<1	<1
pH value	6.00	7.48	8.00
Temperature (°C)	22	18.9	21.6
Turbidity (NTU)	25.4	5.9	8.1
DO (mg/L)	6.60	7.64	7.30
DO Saturation (%)	74%	80%	80%
Suspended Solids (mg/L)	8.0	4.0	2.0

 Name
 Signature
 Date

 Prepared By :
 Lau kai chung
 4/4/2014

Remark or Observation :

Date of Sampling : 7/4/2014

Remark or Observation :

Weather: Cloudy

Monitoring Location	W1	W2	C2
Time (hhmm)	17:00	16:00	17:15
Tide Mode	Mid	-ebb	N/A
Water Depth (m)	<1	<1	<1
pH value	6.30	7.63	6.60
Temperature (°C)	20.9	18.9	21
Turbidity (NTU)	2.80	6.1	1.60
DO (mg/L)	6.90	7.89	7.10
DO Saturation (%)	76%	88%	78%
Suspended Solids (mg/L)	2.0	3.6	2.0

 Name
 Signature
 Date

 Prepared By :
 Lau kai chung
 7/4/2014

Date of Sampling : 9/4/2014

Weather: Sunny

Monitoring Location	W1	W2	C1
Time (hhmm)	9:00	9:50	9:55
Tide Mode		Mid-flood	
Water Depth (m)	<1	<1	<1
pH value	6.30	8.16	8.13
Temperature (°C)	23.9	20.7	20.7
Turbidity (NTU)	2.5	4.1	4.8
DO (mg/L)	5.70	8.25	8.20
DO Saturation (%)	71%	98%	98%
Suspended Solids (mg/L)	2.0	3.4	3.6

Date of Sampling : 11/4/2014

Weather: Cloudy

Monitoring Location	W1	W2	C2
Time (hhmm)	10:23	11:45	16:30
Tide Mode	Mid	-ebb	N/A
Water Depth (m)	<1	<1	<1
pH value	6.30	7.97	6.80
Temperature (°C)	23.2	21.6	24.8
Turbidity (NTU)	2.1	5.0	1.2
DO (mg/L)	7.80	7.45	8.10
DO Saturation (%)	95%	80%	103%
Suspended Solids (mg/L)	2.0	1.0	2.0

 Name
 Signature
 Date

 Prepared By :
 Lau kai chung
 11/4/2014

Date of Sampling : 14/4/2014

Weather: Sunny

Monitoring Location	W1	W2	C2
Time (hhmm)	11:05	13:25	12:04
Tide Mode	Mid	-ebb	N/A
Water Depth (m)	<1	<1	<1
pH value	6.50	8.10	6.60
Temperature (°C)	23.3	21.9	23.1
Turbidity (NTU)	2.0	5.0	1.2
DO (mg/L)	7.80	8.13	7.30
DO Saturation (%)	91%	88%	86%
Suspended Solids (mg/L)	3.0	6.0	3.0

 Name
 Signature
 Date

 Prepared By :
 Lau kai chung
 14/4/2014

Remark or Observation :

Date of Sampling : 16/4/2014

Weather: Sunny

Monitoring Location	W1	W2	C2
Time (hhmm)	13:10	14:30	13:45
Tide Mode	Mid	-ebb	N/A
Water Depth (m)	<1	<1	<1
pH value	6.90	7.73	7.70
Temperature (°C)	24.1	21.4	24.7
Turbidity (NTU)	3.8	4.3	1.7
DO (mg/L)	6.90	7.68	7.10
DO Saturation (%)	81%	80%	84%
Suspended Solids (mg/L)	2.0	3.8	2.0

 Name
 Signature
 Date

 Prepared By :
 Lau kai chung
 16/4/2014

Remark or Observation :

Date of Sampling : 23/4/2014

Weather : Cloudy

Monitoring Location	W1	W2	C1	
Time (hhmm)	10:59	14:00	14:05	
Tide Mode		Mid-flood		
Water Depth (m)	<1	<1	<1	
pH value	7.10	8.37	8.13	
Temperature (°C)	25.5	22.3	22.4	
Turbidity (NTU)	3.8	5.8	2.3	
DO (mg/L)	7.00	8.37	8.41	
DO Saturation (%)	79%	98%	102%	
Suspended Solids (mg/L)	5.0	3.0	1.0	

 Name
 Signature
 Date

 Prepared By :
 Lau kai chung
 23/4/2014

Date of Sampling : 25/4/2014

Remark or Observation :

Weather : Cloudy

Monitoring Location	W1	W2	C2	
Time (hhmm)	14:05	10:40	14:28	
Tide Mode	Mid	-ebb	N/A	
Water Depth (m)	<1	<1	<1	
pH value	7.60	8.18	7.90	
Temperature (°C)	23.4	21.1	23.4	
Turbidity (NTU)	2.3	5.6	2.1	
DO (mg/L)	7.00	8.08	7.10	
DO Saturation (%)	75%	88%	84%	
Suspended Solids (mg/L)	4.0	2.0	2.0	

 Name
 Signature
 Date

 Prepared By :
 Lau kai chung
 25/4/2014

Date of Sampling : 28/4/2014

Remark or Observation :

Weather: Cloudy

Monitoring Location	W1	W2	C2	
Time (hhmm)	11:46	13:00	16:30	
Tide Mode	Mid	-ebb	N/A	
Water Depth (m)	<1	<1	<1	
pH value	7.50	8.17	8.00	
Temperature (°C)	27.2	23.4	28.5	
Turbidity (NTU)	10.7	5.1	9.5	
DO (mg/L)	5.70	8.18	5.9	
DO Saturation (%)	72%	90%	75%	
Suspended Solids (mg/L)	7.0	1.0	3.0	

 Name
 Signature
 Date

 Prepared By :
 Lau kai chung
 28/4/2014

Date of Sampling : 30/4/2014

Weather: Suuny

Monitoring Location	W1	W2	C2	
Time (hhmm)	14:43	14:30	15:07	
Tide Mode	Mid	-ebb	N/A	
Water Depth (m)	<1	<1	<1	
pH value	7.70	7.68	8.00	
Temperature (°C)	24.2	23.1	23.6	
Turbidity (NTU)	4.0	6.2	2.4	
DO (mg/L)	5.70	7.27	6.90	
DO Saturation (%)	66%	75%	80%	
Suspended Solids (mg/L)	2.0	2.2	2.0	

Appendix F: Hydrological Characteristics Monitoring Data

Location	Position	Tide	Date	Time	Weather	Water Depth	Water Flow	Water Flow
Location	rosidon	1100	Duite	11110	,, eutiler	(m)	(m/s)	(m ³ /s)
H1	Mid	Flood	4-Apr-2014	8:45	Cloudy	0.48	0.12	0.150
H1	Mid	Flood	11-Apr-2014	15:10	Cloudy	0.24	0.12	0.150
H1	Mid	Flood	16-Apr-2014					0.000
H1	Mid	Flood	25-Apr-2014	15:10	Cloudy	0.3	0.18	0.225
H2	Mid	Flood	4-Apr-2014	9:15	Cloudy	0.48	0.24	1.507
H2	Mid	Flood	11-Apr-2014	15:40	Cloudy	0.36	0.18	1.130
H2	Mid	Flood	16-Apr-2014					0.000
H2	Mid	Flood	25-Apr-2014	15:40	Cloudy	0.24	0.24	1.507
H1	Mid	Ebb	4-Apr-2014	15:00	Cloudy	0.24	0.18	0.225
H1	Mid	Ebb	11-Apr-2014	10:55	Cloudy	0.12	0.12	0.150
H1	Mid	Ebb	16-Apr-2014	15:10	Sunny	0.18	0.12	0.150
H1	Mid	Ebb	25-Apr-2014	10:00	Cloudy	0.24	0.12	0.150
H2	Mid	Ebb	4-Apr-2014	15:25	Cloudy	0.3	0.18	1.130
H2	Mid	Ebb	11-Apr-2014	11:20	Cloudy	0.18	0.18	1.130
H2	Mid	Ebb	16-Apr-2014	15:45	Sunny	0.24	0.24	1.507
H2	Mid	Ebb	25-Apr-2014	10:30	Cloudy	0.24	0.24	1.507

Appendix G: Landscape and Visual Monitoring Photos





Photo 7 – Chain-link fence was reinstated at the eastern end of Phase 2 works area and covered by canvas sheets. Grass germination was noted in the hydroseeded area applied next to the fence. Photo 8 – No discharge of muddy water was observed in Area C.




Photo 9 – The reinstatement work for the basic nursery utility was still under progress in Phase 1 area of Area B.

Photo 10 – The reinstatement works for the ground of the nursery beds and basic nursery utility were still under progress in both Phases 1 and 2 areas in Area B.







Photo 11 – The soil was washed away from the planting areaPhoto 12 – Some soil which was washed away from thedown to the bottom of the pumping house as observed on 3rdslanting component of the pumping house was removedApril 2014.subsequently.

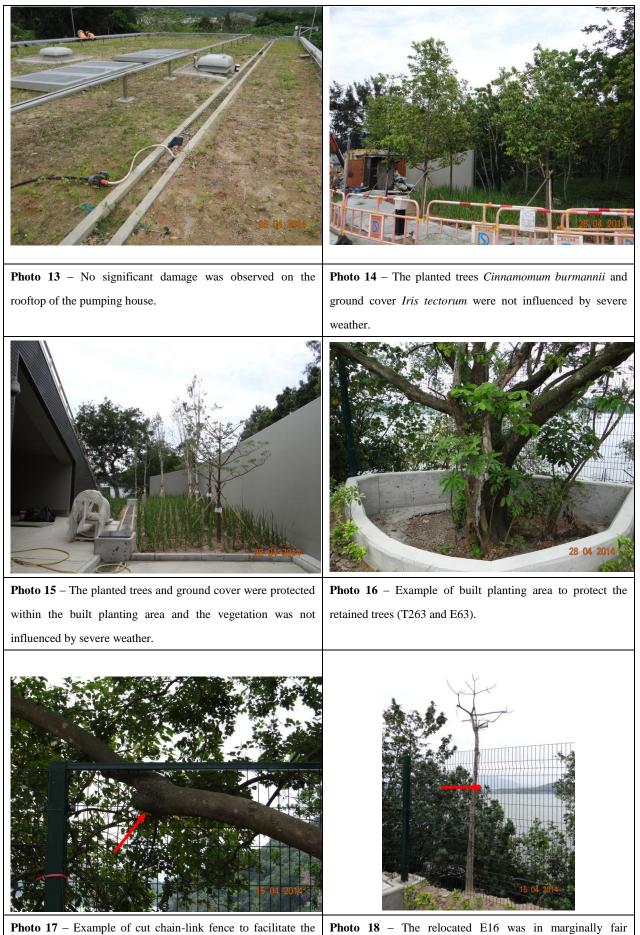

growth of a large scaffold branch of E44.

Photo 18 – The relocated E16 was in marginally fair condition and separated outside the chain-link fence.

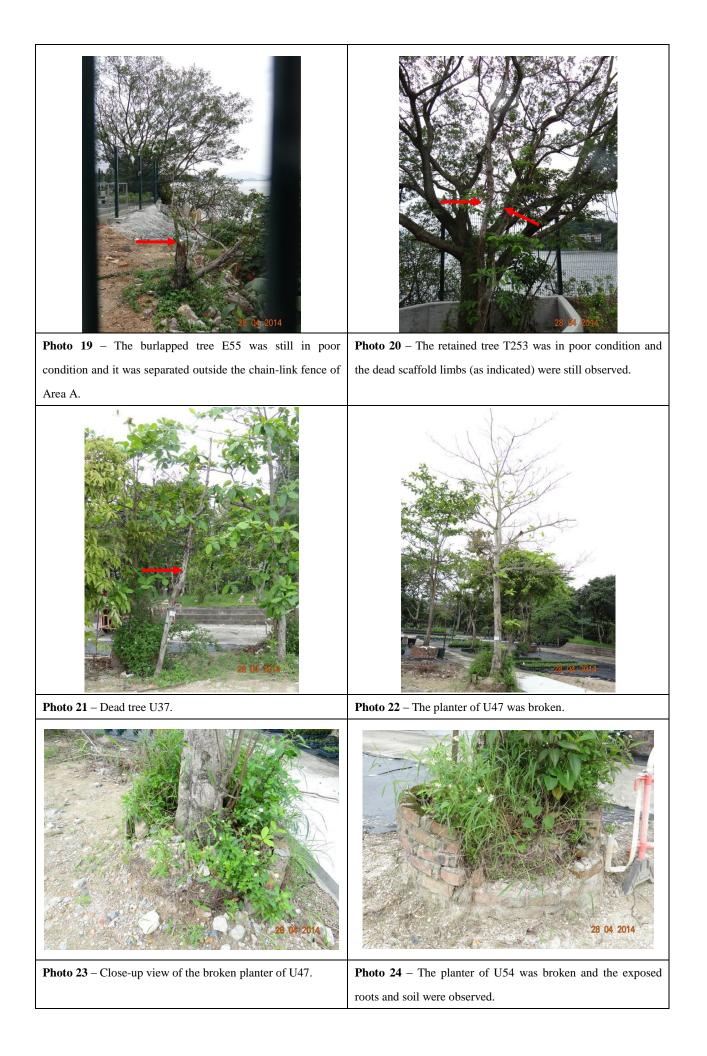

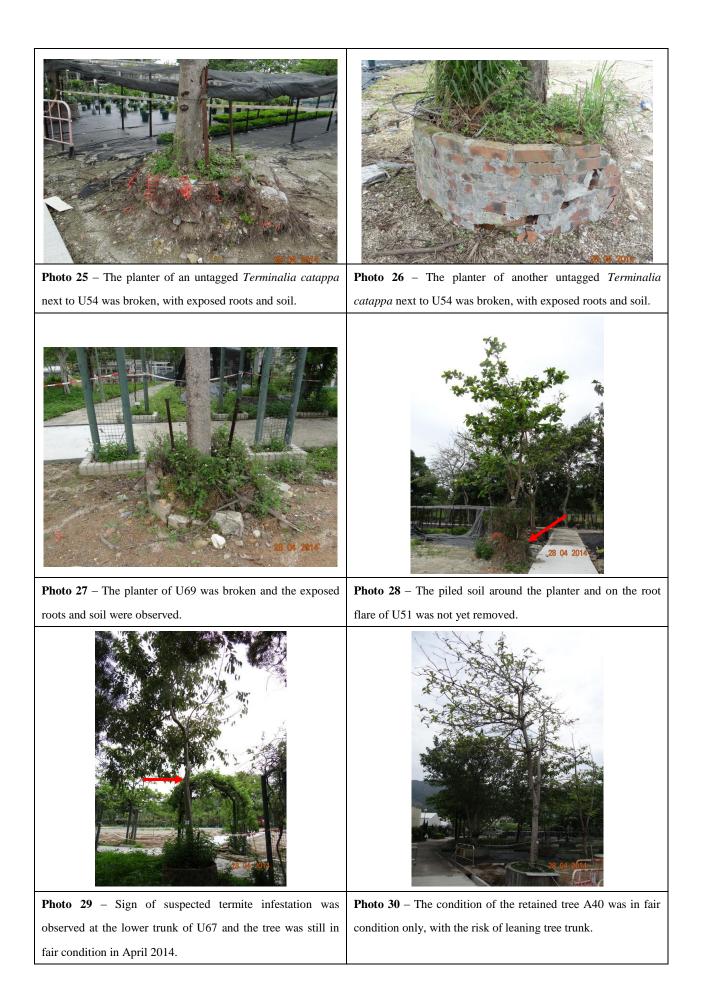



Appendix H:

A)

The recommended mitigation measures of EM&A manual (revision 3)

B)

Implementation status of environmental protection and mitigation measures

A) The recommended mitigation measures of EM&A manual (revision 3)

<u>EIA Ref.</u> A	EM&A Ref.	Recommended Mitigation Measures Noise Impact		Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
S 3.30	2.18	Good Site Practice:	To minimize construction	Contractor	Works areas	Construction	EIAO-TM
		 Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program Mobile plant, if any, shall be sited as far from NSRs as possible 	noise impacts			phase	NCO
		 Machines and plant (such as 					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		trucks) that may be in intermittent					
		use shall be shut down between					
		work periods or shall be throttled					
		down to a minimum					
		 Plant known to emit noise 					
		strongly in one direction shall,					
		wherever possible, be orientated so					
		that the noise is directed away from					
		the nearby NSRs					
		 Material stockpiles and other 					
		structures shall be effectively					
		utilized, wherever practicable, in					
		screening noise from on-site					
		construction activities.					
S 3.31 -	2.19	Use of quieter PME	To minimize construction	Contractor	Works areas	Construction	EIAO-TM
3.32			noise impacts			phase	NCO
S 3.33 –	2.20-2.	Use of temporary noise barrier	To minimize construction	Contractor	Works areas as	Construction	EIAO-TM
3.34	21		noise impacts		shown in Figure	phase	NCO

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
3.36-3.3	2.23-2.				3.5		
8	24						
S 3.35	2.22	Use of alternative quieter	To minimize construction	Contractor	Part of the works	Construction	EIAO-TM
and		construction method (the Low	noise impacts		area for pipe	phase	NCO
Table		Impact Method)			laying in Wai Ha		
3.6					(refer to Figure		
					3.5)		
3.36	2.23-2.	Use of noise enclosure	To minimize construction	Contractor	Part of the works	Construction	EIAO-TM
-3.38	24		noise impacts		area for pipe	phase	NCO
					laying in Wai Ha		
					(refer to Figure		
					3.5)		
В		Air Quality Impact					
S4.16	3.5	Implementation of mitigation	To minimize construction	Contractor	Construction	Construction	EIAO-TM
		measures stipulated in the Air	dust impacts		Sites	Phase	
		Pollution Control (Construction Dust)					
		Regulation and good site practices					
		including but not limited to the					
		following:					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		 Use of regular watering to reduce 					
		dust emissions from exposed site					
		surfaces and unpaved road, with					
		complete coverage, particularly					
		during dry weather;					
		 Use of frequent watering for 					
		particularly dusty static construction					
		areas and areas close to ASRs;					
		 Tarpaulin covering of all dusty 					
		vehicle loads transported to, from					
		and between site location;					
		 Establishment and use of vehicle 					
		wheel and body washing facilities at					
		the exit points of the site;					
		 Routing of vehicles and 					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		positioning of construction plant					
		should be at the maximum possible					
		distance from ASRs.					
		 Stockpiled excavated materials 					
		should be covered with tarpaulin,					
		and should be removed off-site					
		within 24 hours to avoid any odour					
		nuisance arising.					
С		Water Quality Impact					
S5.29	4.5	Construction Site Run-off and	To minimize water quality	Contractor	Works sites	Construction	ProPECC PN 1/94
		Drainage:	impacts			phase	Construction Site
							Drainage
		 Before commencing any site 					
		formation work, all sewer and					
		drainage connections shall be					
		sealed to prevent debris, soil, sand					
		etc. from entering public					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		sewers/drains.					
		 Temporary ditches shall be 					
		provided to facilitate run-off					
		discharge into appropriate					
		watercourses, via a silt retention					
		pond. No site run-off shall enter the					
		fishponds at Shuen Wan.					
		 Sand/silt removal facilities such 					
		as sand traps, silt traps and					
		sediment basins shall be provided to					
		remove sand/silt particles from					
		runoff to meet the requirements of					
		the Technical Memorandum					
		standard under the Water Pollution					
		Control Ordinance. The design of					
		silt removal facilities shall be based					
		on the guidelines provided in					
		ProPECC PN 1/94. All drainage					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		facilities and erosion and sediment					
		control structures shall be inspected					
		monthly and maintained to ensure					
		proper and efficient operation at all					
		times and particularly during					
		rainstorms.					
		 Water pumped out from 					
		excavated pits shall be discharged					
		into silt removal facilities.					
		 During rainstorms, exposed 					
		slope/soil surfaces shall be covered					
		by a tarpaulin or other means.					
		Other measures that need to be					
		implemented before, during, and					
		after rainstorms as summarized in					
		ProPECC PN 1/94 shall be followed.					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		 Exposed soil areas shall be 					
		minimized to reduce potential for					
		increased siltation and					
		contamination of runoff.					
		 Earthwork final surfaces shall be 					
		well compacted and subsequent					
		permanent work or surface					
		protection shall be immediately					
		performed to reduce the potential of					
		soil erosion.					
		 Open stockpiles of construction 					
		materials or construction wastes					
		on-site shall be covered with					
		tarpaulin or similar fabric during					
		rainstorms.					
S5.30	4.7	Further precautionary measures	To minimize water quality	Contractor	Works areas near	Rainy seasons	EIAO-TM
		during rainy season:	impacts to the designated		the Conservation	during	Water Pollution
			Conservation Area		Area	construction	Control Ordinance

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		 For the construction of the box 				phase	(WPCO)
		culvert next to the existing channel					
		of the Wai Ha River, sand bags					
		should be deployed around the					
		boundary of the works trench to					
		prevent muddy water ingress into					
		the adjacent CA or Wai Ha River.					
		Sand bags should also be used to					
		surround the excavated trench.					
		Generally, the sand bags will be					
		placed up to a height of 300mm to					
		provide adequate allowance for the					
		built-up water level during rainstorm					
		event. With sand bags in place,					
		surface runoff will be intercepted					
		and flow to Wai Ha River or					
		collected by the existing drainage					
		system as usual. ■ For the construction of the box					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		culvert in the extreme northeast corner of Shuen Wan Marsh					
		Conservation Area sand bags					
		should be deployed along the limit					
		of the works area to prevent muddy water ingress into the CA. Sand					
		bags should be placed to a height					
		of at least 300mm from ground level and +2.5 mPD (whichever is					
		greater) to provide adequate allowance for the built-up water					
		level during rainstorm events.					
		Unpolluted surface runoff within the					
		works area should then be					
		collected and directed into the					
		existing drainage system.					
		 Sheet-piles, which would be 					
		installed around the works trench					
		near the Conservation Area, would					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		be extended above ground level for					
		about 2m to serve as hoardings to					
		isolate the works site.					
		 Tarpulin sheets would be used to 					
		cover the excavation areas during					
		heavy rainstorms. This would					
		prevent the ingress of rainwater into					
		the trench minimising the risk of					
		muddy water getting into Wai Ha					
		River and the adjacent Conservation					
		Area.					
		 Any concrete washing water 					
		would be contained inside the works					
		site surrounded by the extended					
		sheet piles. A pump sump at the					
		bottom of the trench would be					
		provided to pump any excess water					
		during concrete washing.					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		 Stockpiling the excavated 					
		materials adjacent to the					
		Conservation Area would not be					
		allowed. The excavated materials					
		would be either removed off site					
		immediately after excavation, or					
		stockpile at location(s) away from					
		the Conservation Area. The					
		stockpile locations shall be					
		approved by the site engineer.					
S5.31-S	4.8-4.9	General Construction Activities:	To minimize water quality	Contractor	Works sites	Construction	EIAO-TM
5.32		 Debris and refuse generated 	impacts			phase	WPCO
		on-site should be collected, handled					
		and disposed of properly to avoid					
		entering the Wa Ha River and fish					
		ponds at Shuen Wan. Stockpiles					
		of cement and other construction					
		materials should be kept covered					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		when not being used.					
		 Oils and fuels should only be 					
		used and stored in designated areas					
		which have pollution prevention					
		facilities. To prevent spillage of					
		fuels and solvents to nearby water					
		bodies, all fuel tanks and storage					
		areas should be provided with locks					
		and be sited on sealed areas, within					
		bunds of a capacity equal to 110%					
		of the storage capacity of the largest tank. The bund should be drained					
		of rainwater after a rain event.					
S5.33	4.10	Sewage from Construction	To minimize water quality	Contractor	Works sites	Construction	EIAO-TM
		workforce:	impacts			phase	WPCO
		 Temporary sanitary facilities, 					
		such as portable chemical toilets,					
		should be employed on-site. A					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		licensed contractor would be					
		responsible for appropriate disposal					
		and maintenance of these facilities.					
S5.34	4.11	River Channel Excavation Works:	To minimize water quality	Contractor	Works sites	Construction	EIAO-TM
			impacts			phase	WPCO
		 The excavation works within the 					
		upstream end of the existing river					
		channel of the Wai Ha River for the					
		construction of the proposed box					
		culvert shall be carried out in dry					
		condition. Containment					
		measures such as bunds and					
		barriers shall be used within the					
		affected length of the river channel					
		and the excavation works restricted					
		to within an enclosed dry section of					
		the channel. The excavation works					
		within Wai Ha River shall be					
		restricted to the period from October					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		to April.					
D		Waste Management Implications				1	
S6.20 –	5.5	Good site practices:	To reduce waste	Contractor	Works sites	Construction	ETWB TCW
6.22			management impacts			phase	No.19/2005
		 Nomination of approved 					ETWB TCW
		personnel, such as a site manager,					No.31/2004
		to be responsible for good site					
		practices and making arrangements					
		for collection of all wastes generated					
		at the site and effective disposal to					
		an appropriate facility.					
		 Training of site personnel in 					
		proper waste management and					
		chemical waste handling					
		procedures.					
		 Provision of sufficient waste 					
		disposal points and regular					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		collection for disposal.					
		 Appropriate measures to 					
		minimise windblown litter and dust					
		during transportation of waste by					
		either covering trucks or by					
		transporting wastes in enclosed					
		containers.					
		 Separation of chemical waste for 					
		special handling and appropriate					
		treatment at the Chemical Waste					
		Treatment Facility.					
		 Regular cleaning and 					
		maintenance programme for					
		drainage systems, sumps and oil					
		interceptors.					
		 A Waste Management Plan 					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		should be prepared and submitted to					
		the Engineer for approval. One					
		may make reference to ETWB TCW					
		No. 15/2003 for details.					
		 A recording system for the 					
		amount of wastes generated,					
		recycled and disposed (including the					
		disposal sites) should be proposed.					
S6.23-	5.7	Waste reduction measures:	To achieve waste reduction	Contractor	Works sites	Construction	EIAO-TM
6.24						phase	
		 Segregation and storage of 					
		different types of waste in different					
		containers, skips or stockpiles to					
		enhance reuse or recycling of					
		materials and their proper disposal.					
		 To encourage collection of 					
		aluminium cans by individual					
		collectors, separate labelled bins					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		shall be provided to segregate this					
		waste from other general refuse					
		generated by the work force.					
		 Any unused chemicals or those 					
		with remaining functional capacity					
		shall be recycled.					
		 Maximising the use of reusable 					
		steel formwork to reduce the amount					
		of C&D material.					
		 Proper storage and site practices 					
		to minimise the potential for damage					
		or contamination of construction					
		materials.					
		 Plan and stock construction 					
		materials carefully to minimise					
		amount of waste generated and					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		avoid unnecessary generation of					
		waste.					
S6.25-		Construction & Demolition (C&D)	To minimize off-site disposal	Contractor	Works sites	Construction	EIAO-TM
6.26		Material:	of C&D material			phase	
		Excavated material with suitable	To minimize environmental				
		characteristics/size should be	impacts during the handling				
		reused on-site as fill material as far	of C&D material				
		as practicable, such as for					
		backfilling of the box culvert and					
		drainage pipe works.					
		 Suitable areas should be 					
		designated within the works site					
		boundaries for temporary stockpiling					
		of C&D material.					
		 Within stockpile areas, the 					
		following measures should be taken					
		to control potential environmental					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		impacts or nuisance:					
		- covering material during					
		heavy rainfall;					
		- locating stockpiles to minimize					
		potential visual impacts; and					
		- minimizing land intake of					
		stockpile areas as far as possible.					
		 When disposing C&D material at 					
		a public filling area, the material					
		shall only consist of soil, rock,					
		concrete, brick, cement					
		plaster/mortar, inert building debris,					
		aggregates and asphalt. The					
		material shall be free from marine					
		mud, household refuse, plastic,					
		metals, industrial and chemical					
		waste, animal and vegetable matter,					
		and other material considered to be					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		unsuitable by the Filling Supervisor.					
S6.27		Chemical waste:	To minimize environmental	Contractor	Works sites	Construction	EIAO-TM
		 Contractor should register with 	impacts during the handling,			phase	Waste Disposal
		the EPD as a Chemical Waste	transportation and disposal				(Chemical Waste)
		Producer and to follow the	of chemical waste				(General) Regulation
		guidelines stated in the Code of					
		Practice on the Packaging,					
		Labelling and Storage of Chemical					
		Wastes.					
		 Good quality containers 					
		compatible with the chemical					
		wastes should be used, and					
		incompatible chemicals should be					
		stored separately.					
		 Appropriate labels should be 					
		securely attached on each chemical					
		waste container indicating the					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		corresponding chemical					
		characteristics of the chemical					
		waste, such as explosives,					
		flammable, oxidizing, irritant, toxic,					
		harmful, corrosive, etc.					
		 The Contractor should use a 					
		licensed collector to transport and					
		dispose of the chemical wastes					
		generated at the Chemical Waste					
		Treatment Centre at Tsing Yi, or					
		other licenced facility, in accordance					
		with the Waste Disposal (Chemical					
		Waste) (General) Regulation.					
S6.28		General refuse:	To minimize environmental	Contractor	Works sites	Construction	EIAO-TM
		It should be stored in enclosed	impacts during the handling			phase	
			and transportation of general				
		from C&D material.	refuse				
		 A reputable waste collector 					

EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
		Main Concern to Address	measure?		measure?	measure to
						achieve?
	should be employed by the					
	contractor to remove general refuse					
	from the site, separately from C&D					
	material.					
	An enclosed and covered area					
	is preferred to reduce the					
	occurrence of 'wind blown' light					
	material.					
	Ecological Impact					
6.6	 Sheet-pilings, which will be 	To minimize the impacts on	Contractor	Whole site	Construction	EIAO-TM
	installed around the trench of	the stream and natural river			Phase	
	excavation, should be extended	bank				
	above ground level for ~2m to act as					
	hoarding to isolate the works site.					
	 The trenching works for the 					
	construction of the proposed box					
	culvert should be carried out in					
	phases, with a trench length of not					
	Ref.	Ref. Measures should be employed by the contractor to remove general refuse from the site, separately from C&D material. • An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. • An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. 6.6 • Sheet-pilings, which will be installed around the trench of excavation, should be extended above ground level for ~2m to act as hoarding to isolate the works site. • The trenching works for the construction of the proposed box culvert should be carried out in	Ref. Measures Recommended Measure & Main Concern to Address Should be employed by the contractor to remove general refuse from the site, separately from C&D material. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. Ecological Impact 6.6 • Sheet-pilings, which will be installed around the trench of excavation, should be extended above ground level for ~2m to act as hoarding to isolate the works site. To minimize the impacts on the stream and natural river bank • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in	Ref. Measures Recommended Measure & Main Concern to Address implement the measure? should be employed by the contractor to remove general refuse from the site, separately from C&D material. - An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. - An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. - Contractor 6.6 Sheet-pilings, which will be installed around the trench of excavation, should be extended above ground level for ~2m to act as hoarding to isolate the works site. To minimize the impacts on the stream and natural river bank Contractor • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works f	Ref. Measures Recommended Measure & implement the measure? measure should be employed by the contractor to remove general refuse from the site, separately from C&D material. Implement the measure? Implement the measure? • An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. • An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. To minimize the impacts on the stream and natural river bank Contractor Whole site 6.6 • Sheet-pilings, which will be installed around the trench of excavation, should be extended above ground level for ~2m to act as hoarding to isolate the works site. To minimize the impacts on the stream and natural river bank Contractor Whole site • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box Implement the construction of the proposed box Implement the construction of the proposed box Implement the construction of the proposed box	Ref. Measures Recommended Measure & implement the measure? measure implement the measure? should be employed by the contractor to remove general refuse from the site, separately from C&D material. Implement the measure? Implement the measure? Implement the measure? • An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. • An enclosed and covered area is preferred to reduce the occurrence of wind blown' light material. Implement the impacts on the stream and natural river bank Construction Phase 6.6 • Sheet-pilings, which will be installed around the trench of excavation, should be extended above ground level for ~2m to act as hoarding to isolate the works site. To minimize the impacts on the stream and natural river bank Construction Phase • The trenching works for the construction of the proposed box culvert should be carried out in • The trenching works for the construction of the proposed box culvert should be carried out in Implement the measure?

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		more than 120m in each phase.					
		The trench should be backfilled and					
		compacted with suitable materials					
		upon completion of each phase of					
		the construction works.					
S7.117	6.6	 The construction of intercept 	To minimize the impacts on	Contractor	Whole site	Construction	EIAO-TM
		point of twin cell box culvert at the	the stream and natural river			Phase	
		upstream of Wai Ha River should be	bank				
		confined to only one side of the river					
		bank.					
		 To restore and enhance the 					
		ecological value of the stream, the					
		affected river bank should be					
		reinstated to its original condition or					
		lined with rock-filled gabion.					
		 Planting pits should be provided 					
		in the gabion bank to allow the					
		re-establishment of riparian					
		vegetation.					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
	ļ						achieve?
		 The existing natural riverbed and 					
		substrates should be retained and					
		the natural pool-riffle sequence					
		should be re-created in the new					
		channel bed.					
S 7.118	6.7	 All works carried out within the 	To minimise sedimentation/	Contractor	Whole Site	Construction	EIAO-TM
		the river channel of Wai Ha River	water quality impacts			Phase	
		should be carried out from October					
		to April, with construction carried out					
		by land-based plant.					
		 Works within river/stream 					
		channels should be restricted to an					
		enclosed dry section of the river,					
		with containment measures such as					
		bunds and barriers used within the					
		river to minimize the impacts upon					
		the downstream water body.					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		 Site runoff should be directed 					
		towards regularly cleaned and					
		maintained silt traps and oil/grease					
		separators to minimize the risk of					
		sedimentation and pollution of river					
		water.					
		 The silt and oil/grease separators 					
		should be appropriately designed for					
		the local drainage and ground					
		conditions.					
		 To minimize leakage and loss of 					
		sediments during excavation in					
		narrow channels, tightly sealed					
		closed grab excavators should be					
		deployed where material to be					
		handled is wet.					
S 7.119	6.8	 The construction of the 	To protect plant species of	Contractor/	Whole site	Construction	EIAO-TM
		proposed box-culvert would have the	conservation interest	qualified		Phase	
		potential to directly impact a few		botanist/horticu			

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		individual of a plant species of		lturalist			
		conservation interest (Hong Kong					
		Pavetta, Pavetta hongkongensis).					
		The affected individuals should be					
		transplanted to a suitable nearby					
		habitats prior to the construction					
		phase.					
		 A detailed vegetation survey of 					
		the affected species of conservation					
		interest should be conducted by a					
		suitably qualified botanist/ecologist					
		to identify the affected individuals in					
		order to provide details for					
		transplantation scheme.					
		 Transplantation should be 					
		supervised by a suitably qualified					
		botanist/horticulturalist. A detailed					
		transplantation methodology should					
		be formulated during the detailed					
		design stage of this Project.					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
S 7.120	6.9	 Noise mitigation measures such 	To minimise disturbance	Contractor	Whole site	Construction	EIAO-TM
		as the use of quieter construction	impacts.			Phase	
		plant and temporary noise barriers					
		should be implemented to minimize					
		disturbance to habitats adjacent to					
		the works areas.					
		 Temporary noise barriers should 					
		be used during the construction of					
		the box-culvert along Tung Tsz					
		Road, the floodwater pumping					
		station, the mechanical gate, and					
		drainage pipe to minimize potential					
		construction phase disturbance to					
		ardeids and avifauna foraging in					
		marsh habitat.					
		 Noise generating construction 					
		works near the Shuen Wan Egretry					
		SSSI should be avoided as far as					
		practicable during the breeding					
		season (March to June) of the					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		ardeids.					
		 Works near the SSSI (i.e. 					
		installation of mechanical gate)					
		should be restricted to be executed					
		outside the breeding season by					
		provision of special conditions in the					
		contract document.					
		 Hoardings with minimum height 					
		of 2m should be set up along the					
		south side of the proposed box					
		culvert works area adjacent to the					
		marsh, extending at least 20m at					
		both ends, throughout the					
		construction period.					
S 7.121	6.10	 Placement of equipment or 	To minimise disturbance to	Contractor	Whole site	Construction	EIAO-TM
		stockpile in designated works areas	habitats.			Phase	
		and access routes selected on					
		existing disturbed land to minimise					
		disturbance to natural or					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		moderate-high ecological value					
		habitats.					
S 7.121	6.10	 Construction activities should be 	To minimise disturbance to	Contractor	Whole site	Construction	EIAO-TM
		restricted to work areas that would	natural habitats outside			Phase	
		be clearly demarcated. The work	works area.				
		areas should be reinstated after					
		completion of the works.					
S 7.121	6.10	 Waste skips should be provided 	To minimise disturbance to	Contractor	Whole site	Construction	EIAO-TM
		to collect general refuse and	habitats.			Phase	
		construction wastes. The wastes					
		would be disposed of timely and					
		properly off-site.					
S 7.121	6.10	General drainage arrangements	To minimise sedimentation/	Contractor	Whole site	Construction	EIAO-TM
		should include sediment and oil	water quality impacts			Phase	
		traps to collect and control					
		construction site run-off.					
S 7.121	6.10	 Open burning on works sites is 	To prevent accidental	Contractor	Whole site	Construction	EIAO-TM
		illegal, and should be strictly	hill-fires.			Phase	
		prohibited.					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
S 7.122	6.11	 De-silting should be limited to the 	To minimise sedimentation/	Maintenance	Whole site	Operation	EIAO-TM
		dry season.	water quality impacts	parties of the		Phase	
				channel			
S 7.122	6.11	 Waste material produced during 	To minimise sedimentation/	Maintenance	Whole site	Operation	EIAO-TM
		de-silting should be disposed of in a	water quality impacts	parties of the		Phase	
		timely and appropriate manner.		channel			
S 7.123	6.12	 Planting of trees should be 	To compensate the loss of	Contractor	Whole site	Construction	EIAO-TM
		provided within the project area to	vegetation			Phase	
		compensate for the unavoidable					
		loss of approximately 0.08ha					
		secondary woodland habitat due to					
		the Project.					
		 Planting of trees and other 					
		vegetation within project area along					
		the banks of Wai Ha River and Tung					
		Tsz Road should be carried out to					
		provide compensation for					
		unavoidable tree-felling and loss of					
		riparian vegetation resulting from the					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		Project.					
		 The compensatory planting 					
		should make use of native plant					
		species with flowers/fruits attractive					
		to wildlife.					
S 7.124	6.13	Compensation would be required	To compensate the loss of	Contractor /	The recreational	Construction	EIAO-TM
		for the loss of a small area of marsh	marsh habitat and enhance	qualified	fish pond located	Phase	
		habitat (about 0.30ha) within the CA	the quality compensatory	ecologist	to the southwest		
		resulting from the construction of the	habitat		of the existing		
		box-culvert.			Tung Tsz Nursery		
		 An existing low ecological value 					
		recreational fishpond on government					
		land adjacent to the marsh would be					
		used as a proposed area (about					
		0.8ha) for the compensation for the					
		marsh as well as secondary					
		woodland habitats loss (0.08ha).					
		 The pond should be enhanced 					
		by removing boardwalks around the					

EIA Ref.	EM&A	Recommended Mitigation	Objectives of the	Who to	Location of the	When to	What requirements
	Ref.	Measures	Recommended Measure &	implement the	measure	implement the	or standards for the
			Main Concern to Address	measure?		measure?	measure to
							achieve?
		existing pond, and restoring					
		vegetation along the pond bunds,					
		and it would be re-profiled to provide					
		areas of shallow water					
		(approximately 15-50cm deep),					
		creating a suitable foraging habitat					
		for avifauna, particularly ardeids and					
		other waders.					
		 Screen planting of shrubs and 					
		trees along the south-eastern bund					
		of the pond should be implemented					
		to minimise disturbance to avifauna					
		and other wildlife from the adjacent					
		recreational fishpond. The enhanced					
		pond is expected to provide a					
		moderate-high ecological value					
		wetland habitat.					

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & Main Concern to Address	Who to implement the measure?	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?
F		Landscape and Visual					
Table 8.4	7.6	Visual screen, contaminant/ liaison with nursery, protection of existing trees with works area and construction light are used or practiced to mitigate the impacts during construction phase.	To mitigate the landscape	Contractor	Whole site	Construction	EIAO-TM
Table 8.4	7.7	Viewing area formation, architectural design for pump house, landscape design for pump house, enhancement planting along Tung Tsz Road, sufficient soil depth for enhancement planting, transplanting of trees to adjacent locations, preparation for transplanting and reinstatement of affected area are practiced to mitigate the impacts during operational phase.	To mitigate the landscape and visual impacts during the operational phase.	Contractor	Whole site	Detail Design / Operational Phase	EIAO-TM

Appendix H:

A)

The recommend mitigation measures of EM&A manual (revision 3)

B)

Implementation status of environmental protection and mitigation measures

B) Implementation status of environmental protection and mitigation

EM&A	Recommended	Objectives of the	Location of the	When to implement	What requirements	Implementation status
Ref.	Mitigation Measures	Recommended	measure	the measure?	or standards for the	
		Measure & main			measure to achieve?	
		concern to Address				
	Use well maintained construction					Implemented
	plant		Works areas	Construction phase	EIAO-TM NCO	
	Shut down plants between work					Implemented
	periods	To minimize construction noise				
2.18	Install silencers on construction					Implemented
	equipment					
	Locate mobile plant far away					Implemented
	from NSRs	impact				
	Quiet plants should be used					Implemented
2.19	Use of quieter PME					Not applicable
2.20 - 2.21	Use of temporary noise barrier		Pipe laying in Wai Ha			Not applicable
	Use of alternative quieter		Part of the Works Pipe laying			Not applicable
2.22	construction method		in Wai Ha			
2.23 - 2.24	Use of noise enclosure		Pipe laying in Wai Ha			Not applicable

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & main concern to Address	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?	Implementation status
3.5	Implement regular watering and vehicle washing facilities		Construction Site		EIAO-TM	Implemented
	Cover excavated or stockpile of dusty material by impervious sheeting or sprayed with water	To minimize construction dust impact		Construction phase		Implemented
	Use tarpaulin to cover dusty materials on vehicles					Implemented
4.5	Provide silt trap and oil interceptor to remove the oil, lubricants, grease, silt, grit and debris from the wastewater before pumped to the public storm water drainage system					Implemented
4.5	During rainstorms, exposed slope/soil surfaces shall be covered by a tarpaulin or other means. Others measures that need to be implemented before, during, and after rainstorms as summarized in ProPECC PN 1/94 shall be followed	To minimize water quality impact	Construction Site	Construction phase	EIAO-TM WPCO	Not applicable

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & main concern to Address	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?	Implementation status
4.10	Provide site toilet facilities	To minimize water quality impact	Construction Site	Construction phase	EIAO-TM WPCO	Implemented
4.7	 Further precautionary measures during rainy season: For the construction of the box culvert next to the existing channel of the Wai Ha River, sand bags should be deployed around the boundary of the works trench to prevent muddy water ingress into the adjacent CA or Wai Ha River. Sand bags should also be used to surround the excavated trench. Generally, the sand bags will be placed up to a height of 300mm to provide adequate allowance for the built-up water level during rainstorm event. With sand bags in place, surface runoff will be intercepted and flow to Wai Ha River or collected by the existing drainage system as usual. For the construction of the box culvert in the extreme northeast corner of Shuen Wan Marsh Conservation Area sand bags should be deployed along the limit of the works area to prevent muddy water ingress into the CA. Sand bags should be placed to a height of at least 300mm from round level and +2.5 mPD (whichever is greater) to provide adequate allowance 	To minimize water quality impact to the designated Conservation Area	Works areas near the Conservation Area	Rainy seasons during construction	EIAO-TM WPCO	Not applicable

EM&A	Recommended	Objectives of the	Location of the	When to implement	What requirements	Implementation status
Ref.	Mitigation Measures	Recommended	measure	the measure?	or standards for the	
		Measure & main			measure to achieve?	
		concern to Address				
	for the built-up water level during rainstorm events. Unpolluted surface runoff within the works area should then be collected and directed into the existing drainage system. Sheet-piles, which would be installed around the works trench near the Conservation Area, would be extended above ground level for about 2m to serve as hoardings to isolate the works site. Tarpulin sheets would be used to cover the excavation areas during heavy rainstorms. This would prevent the ingress of rainwater into the trench minimising the risk of muddy water getting into Wai Ha River and the adjacent Conservation Area. Any concrete washing water would be contained inside the works site surrounded by the extended sheet piles. A pump sump at the					
	bottom of the trench would be provided to pump any excess water during concrete					
5.9	Reuse excavated material as much as possible					Implemented
5.7	Any unused chemicals or those with remaining functional capacity shall be recycled.	To achieve waste reduction	Works areas	Construction phase	EIAO-TM	Not applicable
	Recycle scrap metals or abandoned equipment]				Implemented

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & main concern to Address	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?	Implementation status
5.5	A recording system for the amount of wastes generated, recycled and disposed should be proposed Adopt a trip ticket system for the disposal of	To reduce waste	Works areas	Construction phase	ETWB TCW No. 19/2005 ETWB TCW NO. 31/2004	Implemented Implemented
5.11	C&D materials All general refuse should be segregated and stored in enclosed bins or compaction units	management impacts	works areas			Implemented
	Contractor should be a required to register with the EPD as a Chemical Waste Producer and to follow the guidelines states in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and	To minimize the environmental			EIAO-TM	Implemented
5.10	Incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosives, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc.	impacts associated with the handling, transportation and disposal of chemical waste.	Work site	Construction phase	Waste Disposal (Chemical Waste)(General) Regulation	Not applicable

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & main concern to Address	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?	Implementation status
5.5	A recording system for the amount of wastes generated, recycled and disposed should be proposed	To reduce waste management impacts	Works areas	Construction phase	ETWB TCW No. 19/2005 ETWB TCW NO. 31/2004	Implemented
6.6	Sheet-pilings, which will be installed around the trench of excavation, should be extended above ground level for ~2m to act as hoarding to isolate the works site. The trenching works for the construction of the proposed box culvert should be carried out in phases, with a trench length of not more than 120m in each phase. The trench should be backfilled and compacted with suitable materials upon completion of each phase of the construction works.	To minimize the impacts on the steam and natural river bank.	Whole site	Construction phase	EIAO-TM	Implemented
6.6	The construction of intercept oint of twin cell box culvert at the upstream of Wai Ha River should be confined to only one side of the river bank. To restore and enhance the ecological value of the stream, the affected river bank should be reinstated to its original condition or lined with rock-filled gabion. Planting pits should be provided in the gabion bank to allow the re-establishment of riparian vegetation.	To minimize the impacts on the steam and natural river bank.	Whole site	Construction phase	EIAO-TM	No applicable


EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & main concern to Address	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?	Implementation status
	The existing natural riverbed and substrates should be retained and the natural pool-riffle sequence should be re-created in the new channel bed.					
6.7	All works carried out within the river channel of Wai Ha River should be carried out from October to April, with construction carried out by land-based plant. Works within river/stream channels should be restricted to an enclosed dry section of the river, with containment measures such as bunds and barriers used within the river to minimize the impacts upon the downstream water body. Site runoff should be directed towards regularly cleaned and maintained silt traps and oil/grease separators to minimize the risk of sedimentation and pollution of river water. The silt and oil/grease separators should be appropriately designed for the local drainage and ground conditions. To minimize leakage and loss of sediments during excavation in narrow channels, tightly sealed closed grab excavators should be deployed where material to be handled is wet.	To minimize sedimentation/ water quality impacts	Whole site	Construction phase	EIAO-TM	No applicable

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & main concern to Address	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?	Implementation status
6.8	The construction of the proposed box-culvert would have the potential to directly impact a few individual of a plant species of conservation interest (Hong Kong Pavetta, Pavetta hongkongensis). The affected individuals should be transplanted to a suitable nearby habitats prior to the construction phase. A detailed vegetation survey of the affected species of conservation interest should be conducted by a suitably qualified botanist/ecologist to identify the affected individuals in order to provide details for transplantation scheme. Transplantation should be supervised by a suitably qualified botanist/horticulturalist. A detailed transplantation methodology should be formulated during the detailed design stage of this Project.	To protect plant species of conservation interest	Whole site	Construction phase	EIAO-TM	No applicable
6.9	Placement of equipment or stockpile in designated works areas and access routes selected on existing disturbed land to minimize disturbance to natural or moderate-high ecological value habitats.	To minimise disturbance to habitats.	Whole site	Construction phase	EIAO-TM	No applicable
6.13	General drainage arrangements should include sediment and oil traps to collect and control construction site run-off.	To minimise sedimentation/ water quality impacts	Whole site	Construction phase	EIAO-TM	Implemented

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measure & main concern to Address	Location of the measure	When to implement the measure?	What requirements or standards for the measure to achieve?	Implementation status
6.13	Construction activities should be restricted to work areas that would be clearly demarcated. The work areas should be reinstated after completion of the works.	To minimise disturbance to natural habitats outside works area.	Whole site	Construction phase	EIAO-TM	Implemented
6.13	Placement of equipment or stockpile in designated works areas and access routes selected on existing disturbed land to minimize disturbance to natural or moderate-high ecological value habitats.	To minimise disturbance to natural habitats	Whole site	Construction phase	EIAO-TM	Implemented
7.6	Visual screen, contaminant/ liaison with nursery, protection of existing trees with works area and construction light are used or practiced to mitigate the impacts during construction phase	To mitigate the landscape and visual impacts during the Construction phase	Whole site	Construction phase	EIAO-TM	Implemented
7.7	Viewing area formation, architectural design for pump house, landscape design for pump hose, enhancement planting along Tung Tsz Road, sufficient soil depth for enhancement planting, transplanting of trees to adjacent locations preparation for transplanting and reinstatement of affected area are practiced to mitigate the impacts during operational phase.	To mitigate the landscape and visual impacts during the operational phase	Whole site	Detail Design / Operational Phase	EIAO-TM	Not Applicable


Appendix I: Construction Pogramme

								ster Programme (Rev. 6)		
ID no. in 5	Rev. ID no. in Rev 4	ID no. in Rev. 3	ID no. in Re 2	v. Task Name	Duration	Start	Finish	Predecessors	Successors	2010 1st Quarter 2nd Quarter 3rd Quarter 4th
	1		1	Preliminary Works (Area I - Pak Shek Kok)	175 days	Fri 26/2/10	Thu 19/8/10			Jan Feb Mar Apr May Jun Jul Aug Sep Oc
	2 2	2 2	2	Commencement of Works	0 days	Fri 26/2/10	Fri 26/2/10		3,83,88,105	5
		3 3	3	Design & Construction of Site Hoarding	30 days	Fri 26/2/10	Sat 27/3/10	2	4FS-5 days	
	4 4	4 4	4	Site Clearance	10 days	Tue 23/3/10	Thu 1/4/10	3FS-5 days	8FS+10 days,5	
	5	5 5	5	Design of Engineer's Site Office	30 days	Fri 2/4/10	Sat 1/5/10	4	6	5
	6 0	5 6	6	Construction of Engineer's Site Office	60 days	Sun 2/5/10	Wed 30/6/10	5	7	7
	7	7	7	Engineer's Site Office - Setup the Internal Finishing / Furniture/ Equipment	15 days	Thu 1/7/10	Thu 15/7/10	6		
		8 8	8	Construction of Contractor's Accommodation	70 days	Mon 12/4/10	Sun 20/6/10	4FS+10 days	9	2
	9 9	-		Installation of Sewerage Storage Tank	5 days	Mon 21/6/10	Fri 25/6/10	8	10	김 : 🏪 :
	10 10			Contractor Accommodation - Setup the Internal Finishing / Furniture / Equipment	20 days	Sat 26/6/10	Thu 15/7/10	9	11	
	11 1			Establishment of Vehicular Gate, Storage Area Establishment of Welfare Facilities for Workers	15 days	Fri 16/7/10 Sat 31/7/10	Fri 30/7/10 Thu 19/8/10	10	12,13	
	12 1.			Temporary Drainage System	20 days 20 days	Sat 31/7/10	Thu 19/8/10	11		
	15 1.	15		Temporary Drankge of seen	20 utys	bar 517710	1110 19/0/10	11		
	15 15	5 15	15	Time for Completion of Section I	915 days	Fri 26/2/10	Tue 28/8/12			
	16 16	i 16	16	Section I (Area A, B - Shuen Wan)	915 days	Fri 26/2/10	Tue 28/8/12			
	17 1	1 17	17	Commencement of Works	0 days	Fri 26/2/10	Fri 26/2/10		19FS+30 days,35,111,22,20,28	8 🔶 26/2
	18 18	18	18	Preliminary Works	240 days	Fri 26/2/10	Sat 23/10/10			
	19 19			Seek clarification regarding Environmental Permit	30 days	Sun 28/3/10	Mon 26/4/10	17FS+30 days	30	
	20 20			Design of TTA Scheme for Site Access	40 days	Fri 26/2/10	Tue 6/4/10	17	21	
	21 2		21	Submission of TTA to TMLG for Approval	60 days	Wed 7/4/10	Sat 5/6/10	20	25	· · · · · · · · · · · · · · · · · · ·
	22 2			Site Clearance	50 days	Fri 26/2/10	Fri 16/4/10	17	23,26	
	23 22			Project Signboard Hearding Eraction	5 days 40 days	Sat 17/4/10 Thu 22/4/10	Wed 21/4/10 Mon 31/5/10	22	24	
	24 24 25 25			Hoarding Erection Establish Site Access	40 days 30 days	Sun 6/6/10	Mon 31/5/10 Mon 5/7/10	23	25	The fact of the fa
	25 23			Ground Investigation	50 days 75 days	Sat 17/4/10	Wed 30/6/10	24,21	30	
	2	20			15 0035				00	
	28 28	3 28	28	Tree Survey	75 days	Fri 26/2/10	Tue 11/5/10	17	29	J 📑 📰 🖬
	29 29	29	29	Submission of Tree Survey Record	60 days	Wed 12/5/10	Sat 10/7/10	28	30,31	
	30 30		30	Tree Felling	20 days	Mon 26/7/10	Sat 14/8/10	29,139,25,26,19	94,99,37	
	31 3	31	31	Tree Transplanting	90 days	Mon 26/7/10	Sat 23/10/10	29,139	94FS-30 days,99FS-30 days,40FS-30 days	s
	33 33		33	Pumping Station	915 days	Fri 26/2/10	Tue 28/8/12			
	34 34		34	Piling Works	485 days	Fri 26/2/10	Sat 25/6/11	17	10.51.20	
	35 35 36 30			Submission of Method Statement Material Ordering & Delivery to Site	100 days 60 days	Fri 26/2/10 Sun 6/6/10	Sat 5/6/10 Wed 4/8/10	17	46,54,36	
	37 37			Ground Preparation for Piling	10 days	Sun 15/8/10	Tue 24/8/10	139,30	38	· · · · · · · · · · · · · · · · ·
	38 38		37	Preliminary Pile	35 days	Wed 25/8/10	Tue 28/9/10	37,36	39,40	
	39 39			Loading Test	30 days	Wed 29/9/10	Thu 28/10/10	38	55,00	
	40 40			Working Piles	110 days	Wed 29/9/10	Sun 16/1/11	38,31FS-30 days	41	
	40 40			Loading Test for working piles	30 days	Mon 17/1/11	Tue 15/2/11	58,5113-50 days	41	
	42 42		40	Sheetpiling	30 days	Wed 16/2/11	Thu 17/3/11	40	43	
	43 42			Excavation to Pile Cut Off Level / Shoring	100 days	Fri 18/3/11	Sat 25/6/11	42	47	7
	45 45	i 44	43	Main Structure of Pumping Station	815 days	Sun 6/6/10	Tue 28/8/12			
	46 40			Temporary Works Submission	120 days	Sun 6/6/10	Sun 3/10/10	35	47	
	47 4		45	Reinforced Concrete Works	210 days	Sun 26/6/11	Sat 21/1/12	46,43	118SS+80 days,75,48,68,62,74,57	
	48 48			Roofing Manuada Slava	50 days	Sun 22/1/12 Man 12/2/12	Sun 11/3/12	47	49,50	
	49 49			Manmade Slope	50 days	Mon 12/3/12	Mon 30/4/12	48	51	
	50 50			Internal Finishing Works External Finishing Works	70 days 100 days	Mon 12/3/12 Mon 21/5/12	Sun 20/5/12 Tue 28/8/12	48 50,49	51	
	51 5.	. 30	47	LARTIRI I IIIMIII 10185	100 days	191011 211 JI 12	1 UC 20/0/12	30,49	125	9
	53 53	52	51	E & M	815 days	Sun 6/6/10	Tue 28/8/12			
	54 54			Submission of E & M Design	120 days	Sun 6/6/10	Sun 3/10/10	35	55FS-30 days	s T
	55 55			Approval of E & M Design	90 days	Sat 4/9/10	Thu 2/12/10	54FS-30 days	56	
	56 50			Fabrication & Delivery of Plant & Material	415 days	Fri 3/12/10	Sat 21/1/12	55	57	7
	57 57			Plumbing & E&M works	150 days	Sun 22/1/12	Tue 19/6/12	56,47	58FS-30 days	ŝ
	58 58	3 57	56	Final Testing Works	100 days	Mon 21/5/12	Tue 28/8/12	57FS-30 days	125	5
	60 60			External Structure	220 days	Sun 22/1/12	Tue 28/8/12			
	61 61			Pumping Station to Outfall Structure	220 days	Sun 22/1/12	Tue 28/8/12			
	62 62		60	Installation of Cofferdam & Site Hoarding Phase 2	30 days	Sun 22/1/12	Mon 20/2/12	47	63	
	63 63			Excavation	30 days	Tue 21/2/12	Wed 21/3/12	62	64	
	64 64			Construction of 2nos. of 1500mm dia. Drainage Pipes	50 days	Thu 22/3/12	Thu 10/5/12	63	65	
	65 65	5 64	63	2 nos. of Outfall Structures	110 days	Fri 11/5/12	Tue 28/8/12	64	125	4
	67 67	66	65	Tide Level Monitoring Chamber	220 days	Sun 22/1/12	Tue 28/8/12			
	68 68		66	Installation of Cofferdam & Site Hoarding Phase 2	30 days	Sun 22/1/12 Sun 22/1/12	Mon 20/2/12	47	69	<u>a</u>
	69 69		67	Excavation	30 days	Tue 21/2/12	Wed 21/3/12	47	70	
	70 70			Construction of Pipe & Tide Level Monitoring Chambers	50 days	Thu 22/3/12	Thu 10/5/12	69	71	
	71 7			Outfall Structure	110 days	Fri 11/5/12	Tue 28/8/12	70	125	
		10			-10 44/5				123	
	73 73	72	71	External Misc. Works	220 days	Sun 22/1/12	Tue 28/8/12			1 : ÷ :
	74 74			Boundary Wall & Fencing	160 days	Sun 22/1/12	Fri 29/6/12	47	78	8
	75 75	5 74	73	3nos. of Flow Measurement chambers and Pipes	60 days	Sun 22/1/12	Wed 21/3/12	47	76,79	J : :
	76 76			Surface Drainage System & Catchpits	60 days	Thu 22/3/12	Sun 20/5/12	75	77	
	77 7			Concrete Pavement	20 days	Mon 21/5/12	Sat 9/6/12	76	78	
	78 78		77	Landscaping Works	60 days	Sat 30/6/12	Tue 28/8/12	77,74	125	
	79 79			225mm dia. Sewer Across Ting Kok Road and Connection to Existing Manholes	120 days	Thu 22/3/12	Thu 19/7/12	75	80	
	80 80)		Sewer Manhole SM1	40 days	Fri 20/7/12	Tue 28/8/12	79	125	<u>1</u> : : :

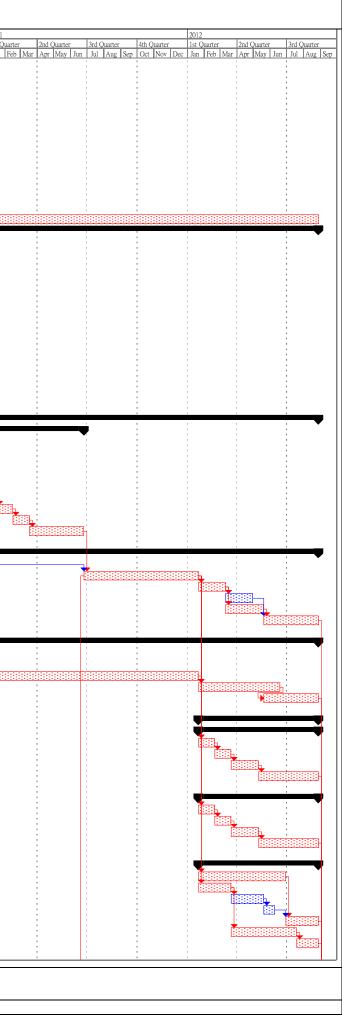

Bit Ub No.the No.the<									Ma	aster Programme (Rev. 6)				
No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No. No.	ID		Rev. ID	no. in Rev. 3		v. Task Name	Duration	Start	Finish	Predecessors	Successors	1st Quarter 2nd Quarter	3rd Quarter	4th Quarter
Image: Section of the section of t	-	82	82	80	70	Twin Cell Box Culvert	915 dave	Eri 26/2/10	Tue 28/8/12			Jan Feb Mar Apr May Jun	Jul Aug Sep	Oct Nov
Image Image <th< td=""><td>-</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>2</td><td>84</td><td></td><td></td><td></td></th<>	-									2	84			
Image Image <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></th<>														
Image: Section of the sectin of the section of the section of th											86			
No. No. <td>1</td> <td>86</td> <td>86</td> <td>84</td> <td>83</td> <td>Condition Survey of Existing Structure</td> <td>15 days</td> <td>Wed 12/5/10</td> <td>Wed 26/5/10</td> <td>85</td> <td>87</td> <td></td> <td></td> <td></td>	1	86	86	84	83	Condition Survey of Existing Structure	15 days	Wed 12/5/10	Wed 26/5/10	85	87			
III III III Junise Crip Tubulization Mail Tubulization Mail Tubulization Mail Tubulization Mail Ma	1	87	87	85	84	Submission of Method Statement to LCSD	60 days	Thu 27/5/10	Sun 25/7/10	86	91		- 西日 - 日本	1
1 0 0 0 Parameter ware frager operations (1) (1) (1) (1) (1) (1) (1) (1) (1) (1)	1	88	88	86	85	Design of Temporary Traffic Arrangement	60 days	Fri 26/2/10	Mon 26/4/10	2	89,90			1
Image: Bit in the state of	1	89	89	87	86	Submission of TTA to TMLG for Approval	90 days	Tue 27/4/10	Sun 25/7/10	88	90FF	1		
1 1 1 Non-Non-Charactering intring Num Num<		90		88	87	Excavation Permit	120 days	Tue 27/4/10	Tue 24/8/10			,		
10 10 10 10 10 10 10 10000 10000 10000 10000 10000 10 10 10 10 10 10 10000 10000 10000 10000 10000 10 10 10 10 10 10000 10000 10000 10000 10000 10 10 10 10 10 10000 10000 10000 10000 10 10 10 10 10 10 10000 10000 10000 10 10 10 10 10 100000 100000 100000 10 10 10 10 1000000 1000000 1000000000 10 10 10 10 1000000000000000000000000000000000000				89	88									1
No. No. <td></td> <td>-</td> <td></td> <td></td> <td>1</td>											-			1
Image: Probability Image: Probab													- I I I	<u>,</u>
9 9														<u>, este i e i e i e i e i e i e i e i e i e i</u>
19 9	-													1
No. No. No. No. Actional Charace 2007													- ·	1
11000	-													
00 <td></td> <td><u>/</u> ///////////////////////////////////</td>														<u>/</u> ///////////////////////////////////
100 100 100 100 100 100 100 100 100 100 000 000 Randian and instanted for ing function, ladius as throw 64 bits 100 bits	-													
Image: 100 Image: 100 <thimage: 100<="" th=""> Image: 100 Image: 1</thimage:>	+													1
Image: Note of the state of	1				97								· · · ·	1
100 106 100 More Story	1											1		1
08 060 0600 0600	1	104	104	102	99	Dia. 2100mm Drainage Pipe	915 days	Fri 26/2/10	Tue 28/8/12					<u> </u>
Interpretation Interpr	1	105	105	103	100	Record Survey	15 days	Fri 26/2/10	Fri 12/3/10	2	106	1 🛃		
198 0.05 0.00 0.00 0.00 0.00 0.0000000 109 0.00 0.00 0.00000000 0.000000000000 0.00000000000000000000000000000000000			106	104		Site Investigation (Trial Pit)	50 days	Sat 13/3/10	Sat 1/5/10		107			1
100 0.00 <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>· · · · · · · · · · · · · · · · · · ·</td><td> · · · · · · · · · · · · · · · · ·</td><td>'</td><td>1</td></th<>											· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · ·	'	1
110 111 111 <td></td> <td></td> <td></td> <td></td> <td></td> <td>Submission of TTA to TMLG for Approval</td> <td>60 days</td> <td></td> <td></td> <td></td> <td>110,109FF</td> <td></td> <td></td> <td>1</td>						Submission of TTA to TMLG for Approval	60 days				110,109FF			1
111 111 110 016 Biologic fragment 66 as Nu 23000 72 0112 112 016 5 Stension fragment 66 as Nu 23000 Nu 23000 11 0113 114 114 114 014					104									-
112 110 100 100 Sdemisan for Approx1 0 days Nor.2001 111 1113 1113 111 111 111 111 111 1113 1111 1113 1111 1113 1111 1111 1113 11111 1111 11111 11111 11111 11111 11111 11111 11111 11111 11111 11111													B	1
103 101 007 Bircharle & Delayer of Personsk 280 dyn Son 20070 Men 2901 112 103 113 114 114 112 108 Men 2901 109,300 113 115 113 113 103 508 Mel 1091 109,300 113 114 116,113 116 116 116 116 116 116 116 1178-30.dyn,1115 11278-30.dyn,1115 11278-30.dyn,1115 11278-30.dyn,1115 11278-30.dyn,1115 11278-30.dyn,1115 11278-30.dyn,1115 1137 113 116 116 116 116 116 116 116 116 116 116 1178-30.dyn,1115 1137 1137 113 116 118 116 118 116 118 116 118 116 118 116 118 116 118 116 118 116 118 116 118 118 118 118 118 118 118 118 118 118 118 118 118 118 118 118 118 118 118						_								<u>.</u>
114 114 112 0.08 MI to be MI to the MI to th														
115 115 113 110 Math Giu MH 60 90 app Txx 89711 Sas 5901 114 116(11) 116 116 110 Math MM 60 150 app Weight MM 70 115 1287.30 day, 2117.50 day, 117 117 117 115 115 Restaurment Math MM 60 61 day Weight MM 81 Sas 12011 105.80 day, 2117.50	_					-								1000
196 116 101 1010 Index 0x1010 150 days Num 6 69711 Web 69711 112 1125711 116 12078-30 days.1218-50 days.171 117 115 115 Restancent of Existing Famic 60 days Wei 149711 38: 171/11 137: 571/11 16 137: 571/11 13	-											I I		<u>19191919191919</u> 1
117 117 118 116 Benatomene di Busing Planer 90 days Thu 201211 Thu 202011 116 116 118 116 111 Milé 55 MH 66												-		
18 138 116 111 Mtl (6 s Mtl (6) 60 avg Weil Moll, Sit 2/11 478.89 dass 198 0 - Tomperportuge Mangement Mun 50 days Man 60411 Sit 3/211 113 Mangement Mun 121 121 113 Mtl (6 s Advanced ID y Saxod) 150 days Taw 4/011 The 1/722 116/85 days 1228 122 123 123 133 Mth (1 s Mtl (1 s Mtl (1 s Mtr (1 s											12013-30 days,12113-30 days,111			1
119 119 119 119 110 1	+					-								1
1010 1010 1111 Index (a wagned in Dry Sawo) 119 days $The 4/011$ $The 1/02$ <td>-</td> <td></td> <td></td> <td>110</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>120</td> <td></td> <td></td> <td>1</td>	-			110							120			1
12 12 10 113 Modifiation of backing Odds Snature of Wait River 190 days Tue 4/011 Tue 1/012 116F8-00 days 122F 121 122 123 124 Installation of social Penatoles 30 days Phi 20/12 Tue 1/012 118F8 123 123 124 124 124 124 124 124 124 124 124 124 124 124 124 124 124 124 124 124 124 125 125 125 125 125 126 126 Completion of Section I 0 days Fit 289/12 7k.124.102.51.58.65.71.84 125 128 128 126 119 Socion II (Acce - E- Ecological Companytion Acre at Share Wat) 365 days Fit 269/10 <	1			118	112									-
123123121 \cdot F. 8. Works120 days $in 22/12$ $in 2/12$ <														
114 124 124 124 124 124 124 124 124 124 125 126 125 126 125 126 125 126 125 126 125 126 125 126 125 126 125 126 125 126 125 126 125 126 125 126 125 126 126 125 126 126 125 126 126 126 125 126 126 126 125 126 126 126 126 125 126 126 126 125 126 1	1													1
125125123116Completion of Section I0 daysTue $288/12$ Tue $288/12$ $78_{124}, 102, 51, 58, 65, 71, 80$ 128128129118Time for Completion of Section II365 daysFri $260/10$ Fri $250/11$	1	123	123	121		E & M Works	120 days	Fri 2/3/12	Fri 29/6/12	122,120	124	.1 1 1		
Image: Note of the second second line of the second line second	1	124	124	122		Misc. Works & Reinstatement	60 days	Sat 30/6/12	Tue 28/8/12	123	125			-
12812812812919Section II (Area C - Ecological Compensation Area at Shuen Wan)365 daysFri 262/10Fri 262/10Sun 11/A/10Fri 262/10Fri 262/10Sun 1/A/10Fri 262/10Sun 1/A/10Sun 1/A/10Fri 262/10Sun 1/A/10Sun 1/A/10Fri 262/10Sun 1/A/10Sun 1/A/10Fri 262/10Sun 1/A/10Sun 1/A/10 <th< td=""><td></td><td>125</td><td>125</td><td>123</td><td>116</td><td>Completion of Section I</td><td>0 days</td><td>Tue 28/8/12</td><td>Tue 28/8/12</td><td>78,124,102,51,58,65,71,80</td><td></td><td></td><td></td><td></td></th<>		125	125	123	116	Completion of Section I	0 days	Tue 28/8/12	Tue 28/8/12	78,124,102,51,58,65,71,80				
128128128129119Social I (Area C - Ecological Compensation Area at Shuen Wan)365 daysFri 262/10Fri 262/10Sam 11/4/10Fri 262/10Sam 12/21Fri 262/10Sam 7/3/10Fri 262/10Sam 7/3/10Sam 7/3/10Fri 262/10Sam 7/3/10Sam 7/3/10Sam 7/3/10S														1
129 129 127 120 Commencement of Works $0 dys$ $Fi 262/10$ $Fi 262/10$ $Fi 262/10$ $Sun 11/410$ 131 131 129 122 $Sin Clearance10 dysFi 262/10Sun 11/410Sun 11/410131131129122Sin Clearance10 dysFi 262/10Sun 11/410Sun 11/410131131129122Sin Clearance10 dysFi 262/10Sun 11/410130131131129123136134131129123136136131121130128137/10130130131131121130131131121130130131131132125Check attual Tald agains Predicted Tidal Level15 dysMn 87/10Mn 87/10Mn 87/10Mn 87/10Mn 87/10Mn 87/10Mn 87/10Mn 11/400133136135133126Survey Existing Pend Bed5 dysMn 87/10Sun 11/410135136136136134127Design of Cleological Compensation Area9 dysSun 11/410Sun 11/410135136136139139130Refer to Penit Requirement plus 15 weeks for Approval and Commencement of Works106 dysMn 267/10Sun 11/410139143F8-60 dys144144139131Fill of$														
130 130 128 121 Preliminary Works 45 days Pri 26/210 Sun 11/4/10 (10) 1131 1131 129 122 Site Clearance 10 days Fri 26/210 Sun 71/10 129 136 1313 1313 131 124 Pumping Water out of Pond 15 days Fri 26/210 Sun 71/10 129 136 133 133 131 124 Pumping Water out of Pond 10 days Fri 26/210 Sun 71/10 129 136 134 134 132 125 Check actual Tidal agains Predicted Tidal Level 15 days Mon 82/10 Fri 12/X10 133 136 136 135 135 136 Garon of Ecological Compensation Area 50 days San 11/4/10 San 11/4/10 133 136 136 136 137 130 Refer to Pernit Requirement plus 15 weeks for Approval and Commencement of Weeks Inf days Mon 22/10 San 11/4/10 San 22/10/10 138 140,114,303,31,71,41,42 140 140														
131131129122Site Clearance10 days \dot{Hi} 26/2/10Sun 7/3/10 (12) (12) (13) 132133133123Hoarding Erection15 days \dot{Hi} 26/2/10 \dot{Sun} 7/3/10 (12) (13) (13) 133131124Pumping Water out of Pend 10 days \dot{Hi} 26/2/10 \dot{Sun} 7/3/10 (12) (13) (13) 134133126Survey Existing Pend leed 15 days $Mon 83/10$ $Mon 23/10$ (13) (13) (13) 135133126Survey Existing Pend Bed 5 days $Mon 83/10$ $Hi 23/10$ (13) (13) (13) 136134127Design of eCological Compensation Area 0 days $Sut 13/10$ $Sun 11/4/10$ (13) (13) (14) 138138136129Submission of Design of Ecological Compensation Area 0 days $Sut 13/10$ $Sun 11/4/10$ (13) (14) 149140143131Fill of Pond to Designed Level (16) days $Mon 26/7/10$ $Sut 23/100$ (13) (14) 141141139131Fill of Pond to Designed Level (16) days $Mon 26/7/10$ $Sut 23/100$ (13) (14) 144144144133Planting Works at Uper Level (6) days $Mon 26/7/10$ $Sut 23/100$ (13) (14) (14) 144144144134Planting Works at Uper Level (6) days $Mon 26/7/10$ <td>-</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>131,132,133</td> <td>26/2</td> <td></td> <td></td>	-										131,132,133	26/2		
132132130123Hearding Erection15 daysFri 26/10Fri 12/101212124Pumping Water out of Pend10 daysFri 26/210Sun 7/3/1012913131314132126Check actual Tichal against Predicted Tidal Level15 daysMone 8/3/10Mone 2/3/10131313131316's 136's 136'						-			1	100	• • •			1
133133113124Pumping Water out of Pond10 daysFri 26/2/10Sun 71/10Sun 71/101239131131134134132125Check actual Tidal against Pedicted Tidal Level15 daysMon 8/3/10Mon 223/10131136685-10 days135133133126Survey Existing Pond Bed5 daysMon 8/3/10Fri 123/10133136136136137127Design of Ecological Compensation Area30 daysSat 13/70Sun 11/1/10135,134FS-10 days,12138138138136129Submission of Design of Ecological Compensation Area to EPD for Approval0 daysSun 11/1/10Sun 11/1/10136139138138136Fill of Pond to Designed Level16 daysMon 267/10Sun 11/1/10138140143141141139132Transplanting Management Plan90 daysMon 267/10Sat 23/10/10139143144145Setting Water Circulation System20 daysFri 7/1/11Sat 52/11144,142144145145143Setting Water Circulation System20 daysFri 7/1/11Sat 52/11144,142144														1
134134132125Check actual Tidal against Predicted Tidal Level15 daysMon 8/3/10Mon 2/3/10Mon 2/3/10131136136/16/5-10 days136135135133126Survey Existing Pond Bed5 daysMon 8/3/10Fri 12/3/101313133136136137127Design of Ecological Compensation Area30 daysSat 13/3/10Sun 11/4/10135,134FS-10 days,12138136138138138138138138138138138138138139130Refer to Permit Requirement plus 15 weeks for Approval and Commencement of Works105 daysSun 11/4/10Sun 11/4/10139140,114,30,31,37,141,142141141138131Fill of Pond to Design of Level165 daysMon 267/10Thu 6/1/111319143FS-60 days141144143133Printogram Drainage Management Plan90 daysMon 267/10Sat 23/10/10139143144144144143133Printing Works at Upper Level90 daysMon 267/10Sat 23/10/10139143144145Setting up Water Circulation System20 days	-					_								1
135135136126Survey Existing Pond Bed5 daysMon 8/3/10Fri 12/3/10133133136136136136134127Design of of Ecological Compensation Area30 daysSat 13/3/10Sun 11/4/10135,134FS-10 days,132138137138136129Submission of Design of Ecological Compensation Area to EPD for Approval0 daysSun 11/4/10Sun 11/4/10136139138138136129Submission of Design of Ecological Compensation Area to EPD for Approval0 dosSun 11/4/10Sun 11/4/10139139139130Refer to Permit Requirement plus 15 weeks for Approval and Commencement of Works105 daysMon 267/10Sun 257/10138140,114,30,31,37,141,142141141139132Transplanting90 daysMon 267/10Sat 23/10/10139145143141133Planting Works at Upper Level90 daysMon 8/11/10Sat 23/10/10139145144144144134Planting Works at Upper Level60 daysMon 8/11/10Sat 52/11143141145145145143Setting up Mater Circulation System20 daysSun 6/2/11Fri 25/2/11144,142144145145145Setting up Mater Circulation System20 daysSun 6/2/11Fri 25/2/11144,142144145145145Setting up Mater Circulation System20 daysSun 6/2/11Fri 25/2/11	╢													-
136138127Design of Ecological Compensation Area30 daysSat 133/10Sun 11/410135,134FS-10 days,132138100101102100100100100100100100138138136129Submission of Design of Ecological Compensation Area to EPD for Approval0 daysSun 11/410Sun 11/4101361318140,114,30,31,37,14,142139139137130Refer to Permit Requirement plus 15 weeks for Approval and Commencement of Works105 daysMon 12/410Sun 25/101318140,114,30,31,37,14,142141141139132Fill of Pond to Designed Level165 daysMon 26/710Sat 23/1010Thu 61/1113991435Fs-60 days141141143143Patning Works at Upper Level60 daysMon 26/710Sat 23/1010Thu 61/11140FS-60 days144143143141133Patning Works at Upper Level60 daysMon 80/710Sat 52/11140,114140FS-60 days144144144143143Patning Works at Lower Level30 daysFir 7/1/11Sat 52/11144,1421441441441431431439 lating works at Lower Level30 daysSin 6/2/11Fir 52/2/11144,142144144144143143Setting up Water Circulation System20 daysSin 6/2/11Fir 52/2/11144,1421441451441431435 setting up Water	-													
Image: Normal SectionImage: Normal Sectio	1													1
139130Refer to Permit Requirement plus 15 weeks for Approval and Commencement of Works105 daysMon 12/4/10Sun 25/7/10San 25/7/11San 25/7/11 <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>,</td><td>130</td><td>l bistal</td><td></td><td>1</td></th<>										,	130	l bistal		1
139130Refer to Permit Requirement plus 15 weeks for Approval and Commencement of Works105 daysMon $12/4/10$ Sun $257/10$ Sun $257/10$ 103 13140(114,30.3)(3,7)(4),142140140138131Fill of Pond to Designed Level165 daysMon $267/10$ Thu $61/11$ 139143FS-60 days141141139132Transplanting90 daysMon $267/10$ Sat $231/010$ 139143FS-60 days14214214133Planting Works at Upper Level90 daysMon $267/10$ Sat $231/010$ 139145143141133Planting Works at Lower Level60 daysMon $801/10$ Thu $61/11$ 140FS-60 aps145144144142134Planting Works at Lower Level30 daysFri $71/11$ Sat $52/11$ 141143145145145143135Setting up Mater Circulation System20 daysSun $6/211$ Fri $25/211$ 144,412144	1	138	138	136	129	Submission of Design of Ecological Compensation Area to EPD for Approval	0 days	Sun 11/4/10	Sun 11/4/10	136	139	↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓		1
140141138131Fill of Pond to Designed Level165 daysMon 267/10Thu 61/11139143FS-60 days141141139132Transplanting90 daysMon 267/10Sat 231/010139	1										140,114,30,31,37,141,142	[:::::::::::::::::::::::::::::::::::::	all '	1
142 143 143 Temporary Drainage Management Plan 90 days Mon 267/10 Sat 23/10/10 133 143 143 143 143 Planting Works at Upper Level 60 days Mon 8/11/10 Thu 6/1/11 140FS-60 days 144 144 144 142 134 Planting Works at Lower Level 30 days Fri 7/1/11 Sat 52/11 143 145 145 145 143 Setting up Water Circulation System 20 days Sin 6/2/11 Fri 25/2/11 144,142 146	1											and the second sec		
143 143 143 Planting Works at Upper Level 60 days Mon 8/11/10 Thu 6/1/11 140FS-60 days 144 144 144 142 134 Planting Works at Lower Level 30 days Fri 7/1/11 Sat 50/11 143 145 145 145 143 135 Setting up Water Circulation System 20 days Sun 6/2/11 Fri 25/2/11 144,142 146	1	141	141	139	132	Transplanting	90 days	Mon 26/7/10	Sat 23/10/10	139		1 : :		
144 144 142 134 Planting Works at Lower Level 30 days Fri 7/1/1 Sat 5/2/1 143 145 145 145 143 135 Setting up Water Circulation System 20 days Sin 6/2/11 Fri 25/2/11 144,142 146]	142	142				90 days	Mon 26/7/10	Sat 23/10/10	139	145			<u> </u>
145 143 135 Setting up Water Circulation System 20 days Sun 6/2/11 Fri 25/2/11 144,142 146														- 400
146 146 146 136 Completion of Section II 0 days Fri 25/2/11 Fri 25/2/11 145											146		,	1
		146	146	144	136	Completion of Section II	0 days	Fri 25/2/11	Fri 25/2/11	145		1 : :		<u>:</u>


Master Programme - Rev. 6 Data Date: 2010-2-26	Task Critical Task		•	Summary Rolled Up Task	Rolled Up Critical Task	 Rolled Up Progress Split		External Tasks Project Summary	 Group By Summary Deadline	↓
						Page	2			

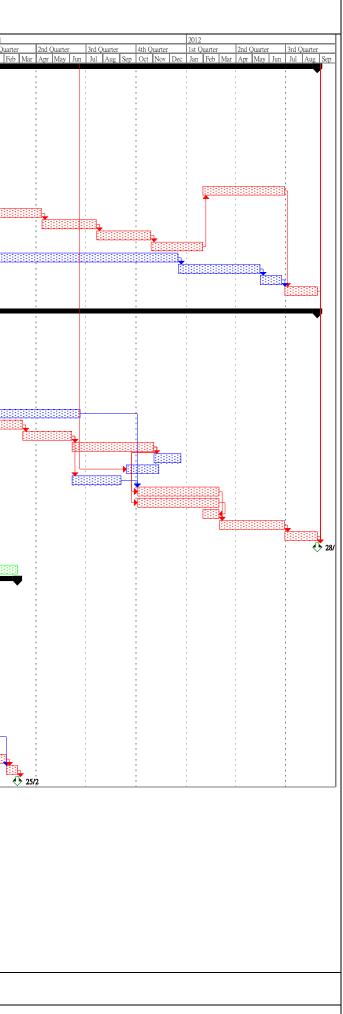



Appendix J: Three month rolling programme


	Contract Title: Drainage Im	Contract No.: DC/2 provement Works	2009/22 in Shuen Wan,	Tai Po - Contract 1		
		rogramme for Outs				
ID	Task Name		Duration	Start	Finish	
1	Outstanding Works at Shuen Wan		90 days	Apr 7 '14	Jul 5 '14	Apr May Jun Jul Au
2						
3	Area A	······································	90 days	Apr 7 '14	Jul 5 '14	
4	Minor rectification of Defects at Pump station		90 days	Apr 7 '14	Jul 5 '14	
5	Minor rectification works along Ting Kok Road		60 days	Apr 7 '14	Jun 5 '14	
6			••••		••••	
7	Area B		90 days	Apr 7 '14	Jul 5 '14	
8	Reinstatement Works		90 days	Apr 7 '14	Jul 5 '14	
9		······································			······	
10	Area C		0 days	Apr 7 '14	Apr 7 '14	• 4/7
11	Completed and handed over to DLO for Maintenance		0 days	Apr 7 '14	Apr 7 '14	♦ 4/7
		No				. A
	Task	Rolled Up	Task		External Tasks	
	Critical Task		Critical Task		Project Summary	
	Progress	Rolled Up	Milestone	\diamond	Group By Summary	
	Milestone 🔶	Rolled Up	Progress		Deadline	
	Summary	Split				
		Page 1				


Appendix K: Graphical plots of trends of monitored parameter

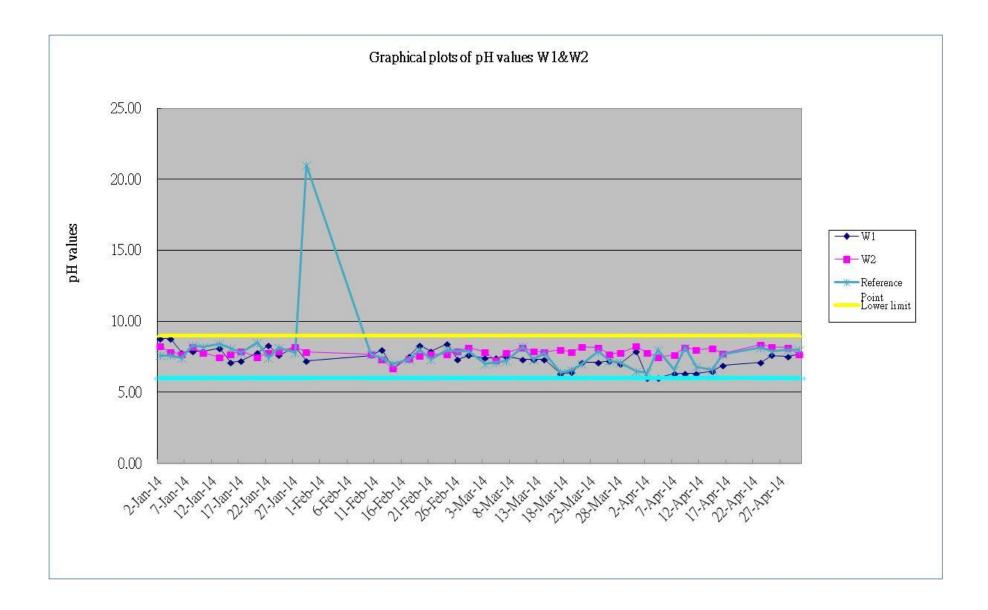


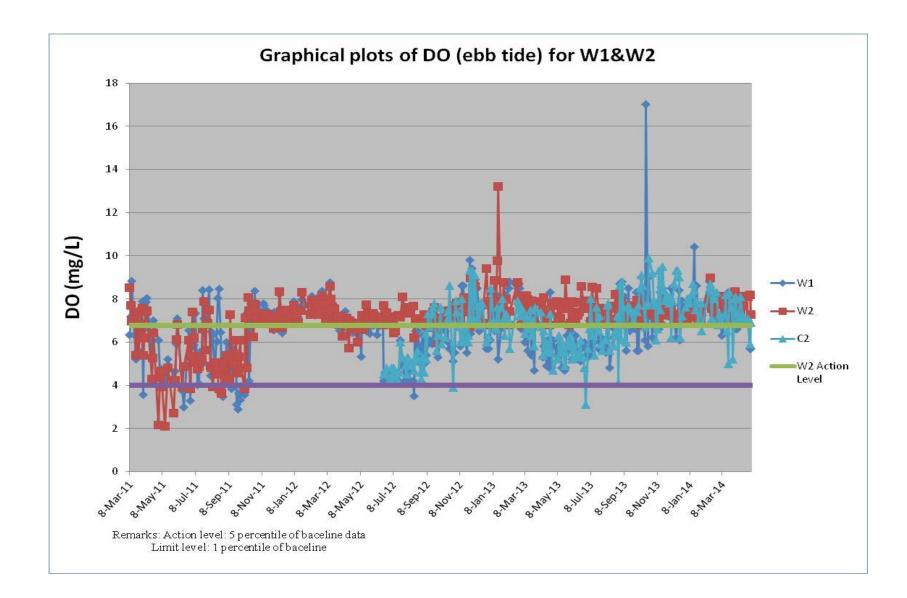


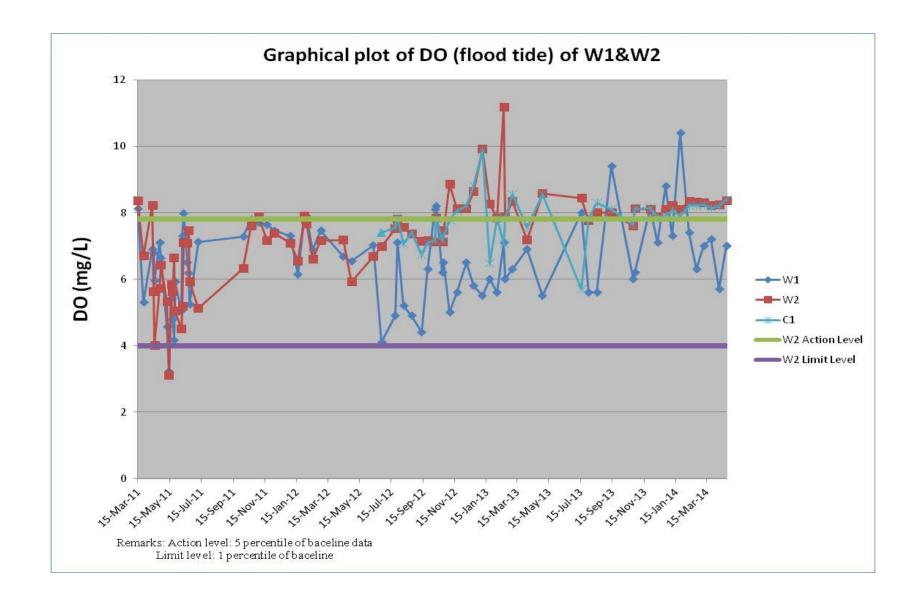


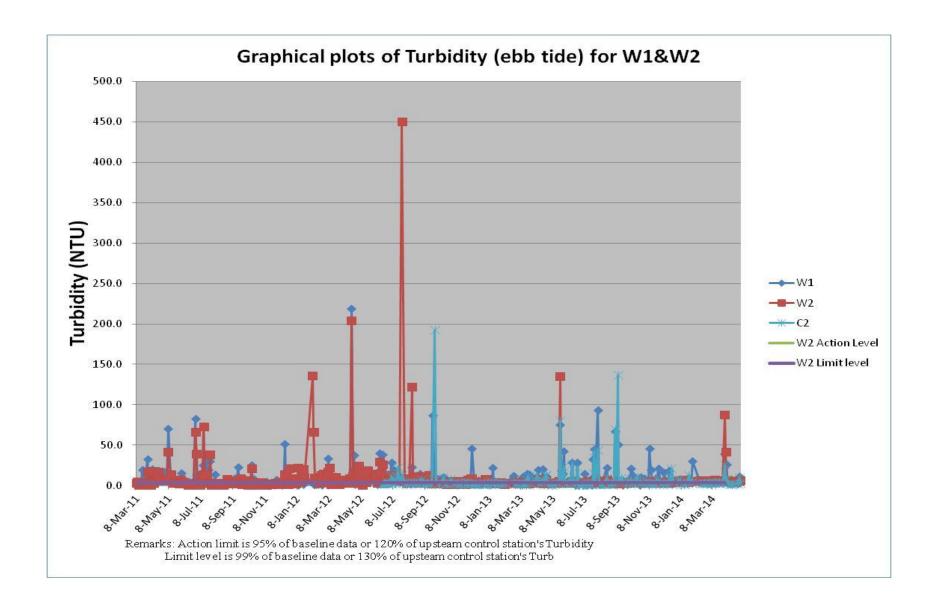


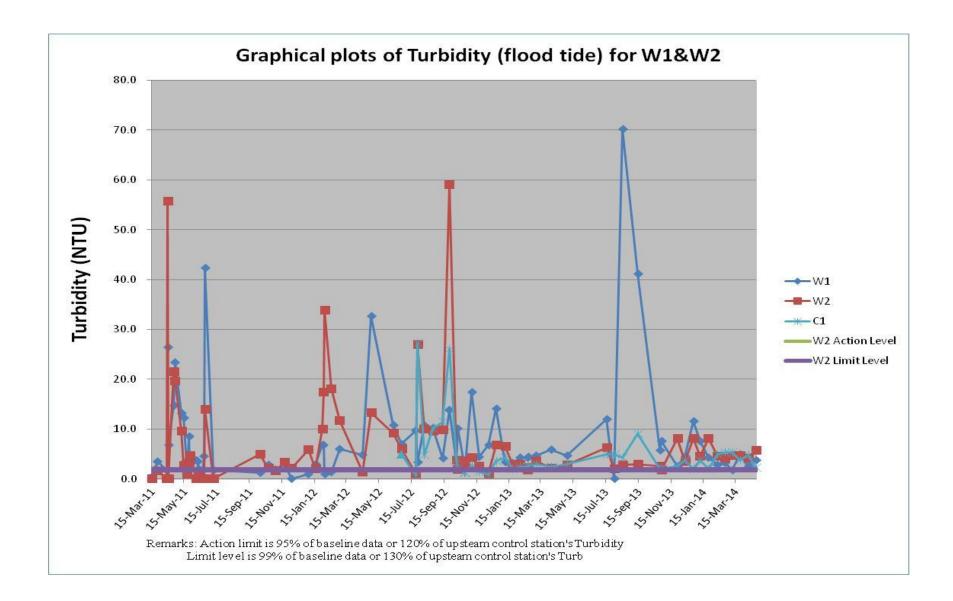


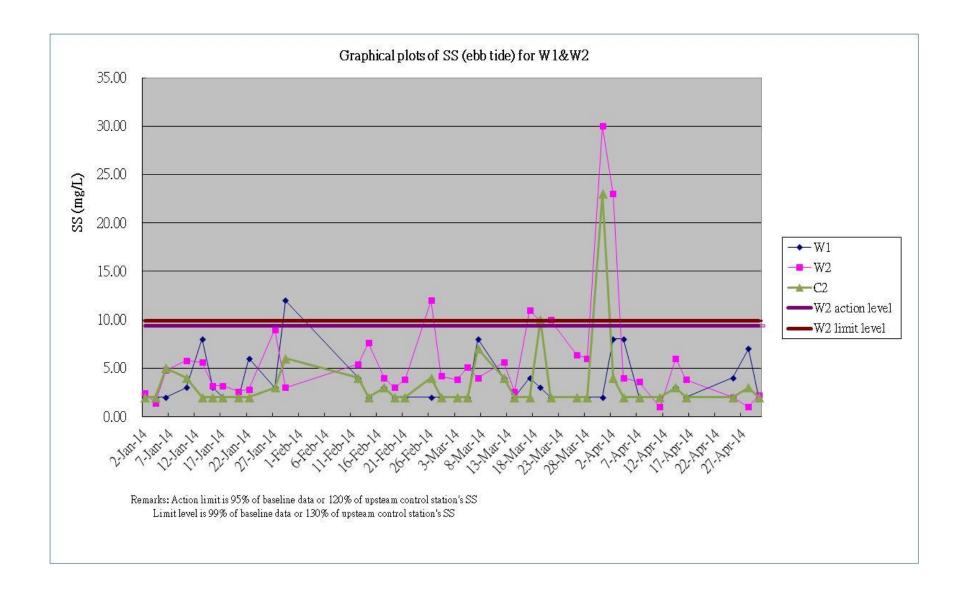


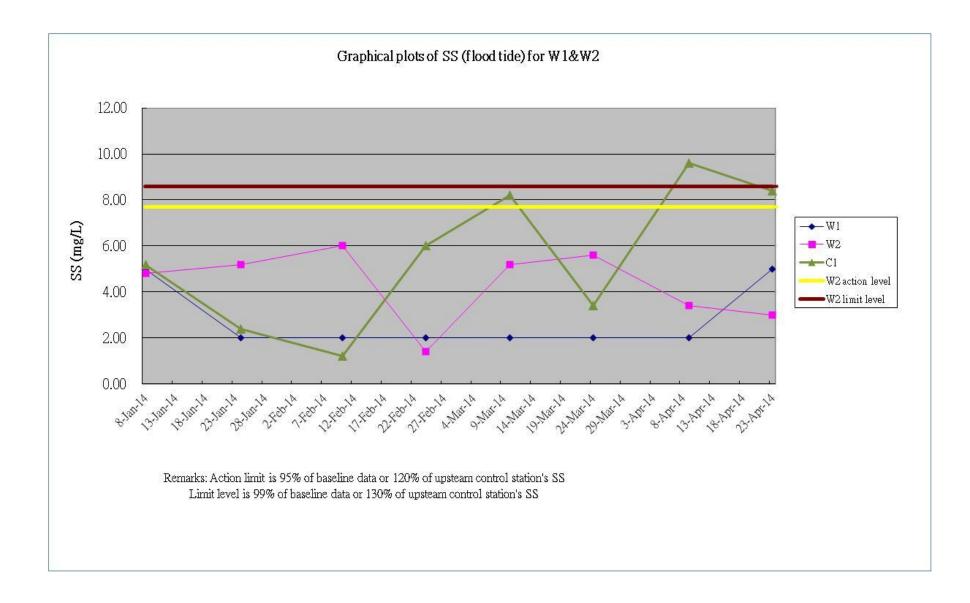


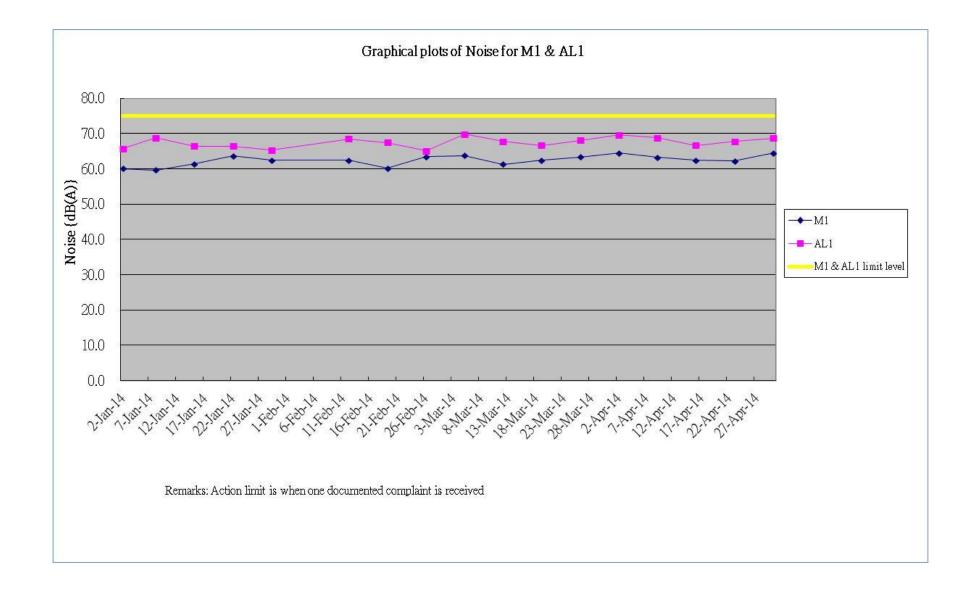

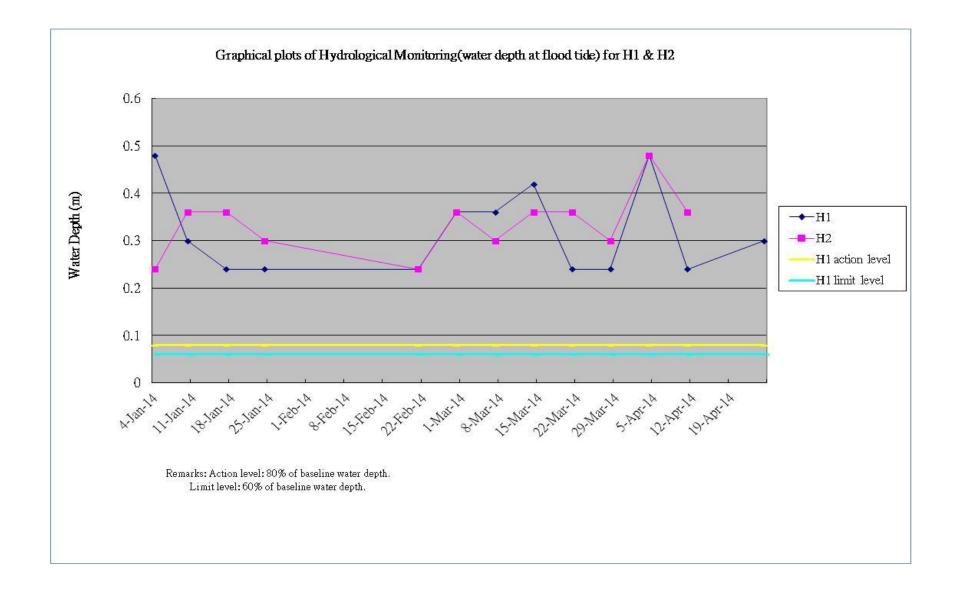

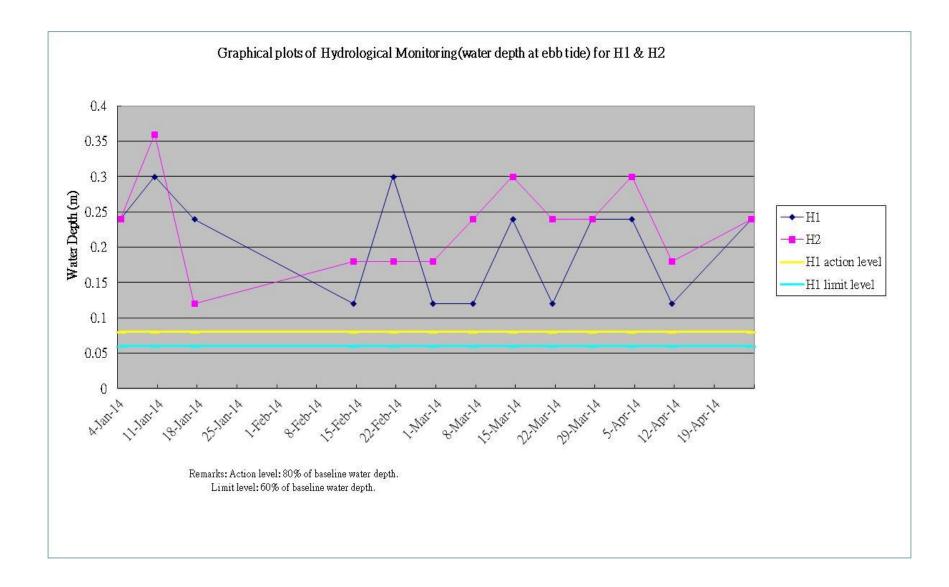

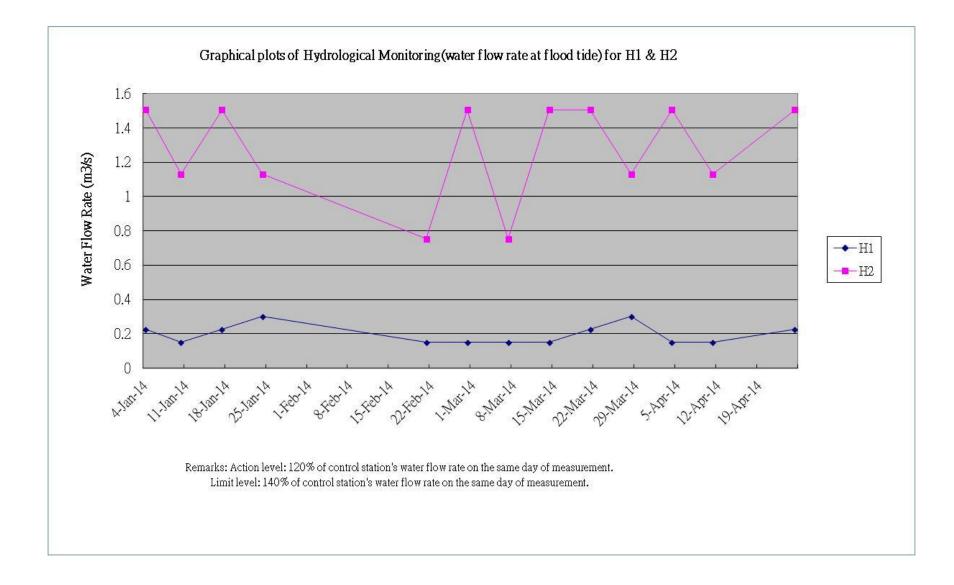

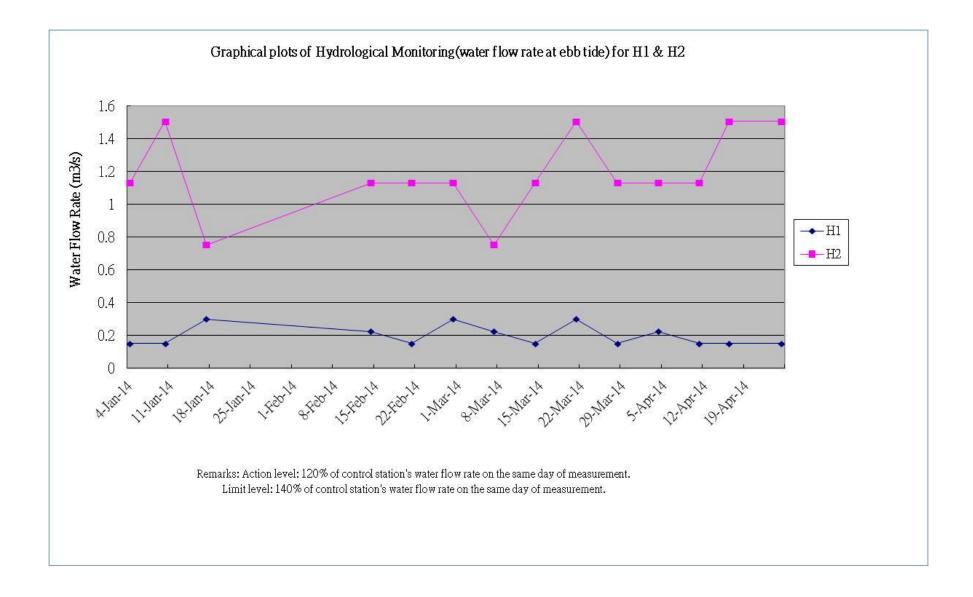

Appendix L: Photo of Wai Ha River in April 2014

