Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.

Ref No.: 100440EN131181

Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk



### Contract No. EP/SP/58/08

### **Sludge Treatment Facilities**

### **Quarterly Environmental Monitoring and Audit Report**

For

### September 2013 to November 2013

Report No.: 100440EN131181

Certified by John K. M. Ho (Environmental Team Leader)

Date

23 December 2013

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Ref No.: 100440EN131181

# CONTENTS

1.	Executive Summary
2.	Introduction
3.	General Review
4.	Construction Phase Environmental Monitoring and Audit
5.	Summary of Complaints, Summons and Successful Prosecutions
6.	Comments and Conclusions for September 2013 to November 2013
Appendices:	
Appendix 1:	Environmental Mitigation Implementation Schedule
Appendix 2:	Summary of Ecology Monitoring
Appendix 3:	Summary of Landscape and Visual Impact Survey
Appendix 4:	Summary of Waste Flow
Appendix 5:	Event / Action Plan for Water Quality
Appendix 6:	Figures
Appendix 7:	Work Program
List of Tables:	
Table 3.1	Summary of Monitored Parameters
Table 3.2	Action and Limit Levels for Marine and Stream Water Quality
Table 3.3	Action Level for Landfill Gas Measurement
Table 4.1	Summary of Environmental Monitoring from September 2013 to
	November 2013
Table 4.2	Summary of Landfill Gas Monitoring
Table 4.3	Construction Activity Undertaken during September 2013 to
	November 2013
Table 5.1	Summary of Environmental Complaints and Prosecutions
List of Figures:	
Figure 1.1	WENT Landfill Control Zone
Figure 3.1	Location of Project Site
Figure 3.2	Project Organisation Structure

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Ref No.: 100440EN131181

### 1. Executive Summary

The requisite construction works for the Environmental Protection Department Contract No. EP/SP/58/08 Sludge Treatment has commenced construction activity on 22 December 2010. The requisite impact environmental monitoring comprising of water quality, landfill gas, ecology, landscape and visual impact was conducted throughout this reporting quarter.

### Air Quality and Noise Level

Accordance to EIA study, there is no sensitive receiver for air and noise located nears the construction area and hence dust and noise monitoring is not required.

### Stream Water Quality

Pursuant to Clause 5.7.1.1 of the EM&A Manual, impact water quality monitoring shall be carried out during site formation, piling and construction of the access road. As the above mentioned site construction has been completed on 17 August 2012 (four weeks post monitoring was commenced by 20 August 2012 and ended on 14 September 2012 inclusively), so that stream water quality monitoring was not required in the reporting period.

### Marine Water Quality

Marine water quality monitoring was not required in the reporting period.

### Landfill Gas Monitoring

Excavation works has been carried out within the WENT landfill consultation zone in the reporting period. Landfill gas monitoring was carried out by a competent person during the excavation, operation in chamber and confined space within the WENT landfill control zone and no exceedance was found.

### <u>Ecology</u>

Routine ecology monitoring was carried out throughout the reporting quarter.

### Landscape and Visual Monitoring

Monitoring of landscape and visual impact was conducted to ensure compliance with the intended aims of the measures and the effectiveness of the mitigation measures.

### <u>Complaints</u>

As far as the complaint on the construction work in respect of environmental protection and pollution control was concerned, there was no complaint received during this reporting quarter.



Ref No.: 100440EN131181

### 2. Introduction

Tuen Mun, N.T.,

Hong Kong.

This quarterly report reviews the progress of the environmental monitoring and audit work associated with Contract No. EP/SP/58/08 Sludge Treatment Facilities in Nim Wan for the twelfth quarter of construction activity from 25 August 2013 to 24 November 2013.

Since water quality monitoring was not required in the reporting period, no graphical presentation for marine and stream water quality results for the reporting period is included.

Summary of ecology monitoring, landscape and visual impact monitoring are attached in Appendix 2 and 3 respectively. Comments and conclusions for this reporting quarter are included.

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Ref No.: 100440EN131181

### 3. General Review

3.1 Background

The Contractor, VW-VES (HK) Limited, has been awarded a contract by the Environmental Protection Department of the Government of the Hong Kong Special Administrative Region for the Sludge Treatment Facilities. The location of the site is shown in Figure 3.1.

The program commenced in November 2010 and is anticipated to complete in 2013.

The construction schedule will be based on the major works associated with the project. The major works under this contract include:

Incineration Plant

- a) Sludge receiving, storage and feeding system
- b) Fluidized bed incinerators
- c) Waste heat recovery and power generation system
- d) Flue gas treatment system
- e) Ash storage and handling system
- f) Residue storage and handling system
- g) Fluidized bed sand storage and handing system
- h) Reagent reception and storage system
- i) Process control and monitoring system

### Ancillary and Supporting Facilities

- a) Weighbridge
- b) Site security
- c) Administration building
- d) Vehicle washing facilities
- e) Maintenance workshop and utility yard
- f) Drainage system
- g) Sewerage system
- h) Sewage treatment works
- i) Water supply system
- j) Deodorization system

The project organisation with respect to environmental protection works is shown in Figure 3.2, which indicates responsibilities and lines of communication of the various parties concerned.



Ref No.: 100440EN131181

3.2 Summary of Environmental Monitoring and Audit (EM&A) Requirements

The EM&A program requires the monitoring of water quality prior to the commencement of and during the construction. A baseline report was prepared in December 2010 for the contract based on monitoring data acquired before the commencement of construction works.

Impact monitoring of water quality is to be undertaken at the designated monitoring stations. The monitored parameters are summarized in Table 3.1.

Action and Limit (AL) levels are established based on the data from the baseline report. Should the monitoring results indicate any non-compliance of AL levels, actions according to the Event / Action Plan in Appendix 5 are to be followed and appropriate environmental mitigation measures as in Appendix 1 are to be implemented to rectify the situation. The implementation status of mitigation measures is also shown in Appendix 1.

Impact ecology and visual survey monitoring are to be conducted at the construction area on regular basis. Monitoring parameters are tabulated in Table 3.1.

Landfill gas monitoring is required whenever there is excavation deeper than 300mm or works conducted in confined space within the WENT Landfill Consultation Zone (see Figure 1.1).

The Contractors (VW-VES (HK) Limited) is responsible for waste control within the construction site, removal of the waste material produced from the site and to implement any mitigation measures to minimize waste or redress problems arising from the waste from the site. The waste material may include any sewage, waste water or effluent containing sand, cement, silt or any other suspended or dissolved material to flow from the site onto any adjoining land, storm sewer, sanitary water, or any waste matter or refuse to be deposited anywhere within the site or onto any adjoining land.

The Contractor shall also pay attention to the Waste Disposal Ordinance, the Dumping at Sea Ordinance, the Public Health and Municipal Services Ordinance and the Water Pollution Control Ordinance, and carry out the appropriate waste management work. The relevant licence / permit, such as the effluent discharge licence, the chemical waste producer registration, etc. shall be obtained. The Contractor shall refer to the relevant booklets issued by EPD when applying for the licence / permit.

The environmental mitigation measures and status for waste management are summarized in Appendix 1.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.

: +852-2450 8233 Tel Fax : +852-2450 6138 : matlab@fugro.com.hk E-mail Website : www.materialab.com.hk



Ref No.: 100440EN131181

able 3.1	Summary	/ of	Monitored	Parameters

Table 3.1	Summary of Mon	itored Parame	ters	
Parameters	Monitored Items	Number of Stations	Frequency	Requirement
Marine water	<ul> <li>Cadmium</li> <li>Chromium</li> <li>Aluminium</li> </ul>	2 monitoring stations and 1 control station	Three days per week for mid-ebb and mid-flood tides during foundation piling of the STF	Sampling is taken at three water depths, namely, 1m below water Surface, mid- depth and 1m above sea bed, except where the water depth be less than 6m, in which case the mid- depth station may be omitted. Shall the water depth be less than 3m, only the mid-depth station will be monitored.
Stream water	<ul> <li>pH</li> <li>Turbidity</li> <li>Suspended solids</li> <li>Dissolved oxygen</li> </ul>	3 monitoring stations and 2 control stations	Three days per week for mid-ebb and mid-flood tides during site formation and foundation piling of the STF and construction of the access road	<ul> <li>Two consecutive measurements of DO concentration, DO saturation, turbidity and pH are taken at mid- depth at each location.</li> <li>Water samples for SS measurement is collected at the same depth at each location.</li> </ul>
Ecology	Site condition and bird monitoring	Whole Middle Lagoon and 20m from the boundary of the Lagoon	<ul> <li>Monthly monitoring for avifauna</li> <li>Habitat monitoring at least twice per month</li> <li>Monthly vegetation monitoring</li> </ul>	<ul> <li>Avifauna and their behavior.</li> <li>All birds seen and heard should be identified and counted.</li> <li>Signs of breeding of birds.</li> <li>Coverage of water and PFA filling activities in Middle Lagoon.</li> </ul>
Landscape and Visual Impact	All measures, including compensatory planting, undertaken by both the Contractor and the specialist Landscape Sub- Contractor	East Lagoon	Biweekly	Ensure compliance with the intended aims of the measures and the effectiveness of the mitigation measures.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.

: +852-2450 8233 Tel : +852-2450 6138 Fax E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk



Ref No.: 100440EN131181

Table 3.1	(Con't)			
Parameters	Monitored Items	Number of Stations	Frequency	Requirement
Landfill gas	<ul> <li>Oxygen</li> <li>Methane</li> <li>Carbon dioxide</li> </ul>	Excavation, operation in chamber and confined space within the WENT Landfill Control Zone. (See Figure 1.1)	During the construction and operation	<ul> <li>Excavation between 300mm to 1m deep:         <ul> <li>Directly after the excavation has been completed.</li> <li>Periodically whilst the excavation remains open.</li> </ul> </li> <li>Excavation deeper than 1m:         <ul> <li>At ground surface before excavations commences.</li> <li>Immediately before any worker enters the excavation.</li> <li>At the beginning of each working day for the entire period the excavation remains open.</li> <li>Periodically whilst the excavation remains open.</li> </ul> </li> </ul>

#### 3.3 Action and Limit Levels

## Water Quality Limit

Environmental auditing on the monitoring data is to be undertaken based on the Action and Limit (AL) levels for water quality to check against any non-compliances.

The AL levels for monitored parameters are formulated from the baseline monitoring data. The AL levels for marine and stream water quality are tabulated in Table 3.2.

Parameters	Action Level	Limit Level
DO in mg/L	≤ 5.16	≤ <b>4</b>
(mid-depth)		
SS in mg/L	≥ 41 <u>AND</u> 120% of control	≥ 85 AND 130% of control
(mid-depth)	station's SS on the same day	station's SS on the same day
	of measurement	of measurement
Turbidity in NTU	≥ 36.4 <u>AND</u> 120% of control	≥ 78.9 AND 130% of control
(mid-depth)	station's turbidity on the	station's turbidity on the
	same day of measurement	same day of measurement
рН	pH ≤7.55 or pH ≥ 8.11	$pH \leq 6 \text{ or } pH \geq 9$

Table 3.2 Action and Limit Levels for Marine and Stream Water Quality

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel	: +852-2450 8233
Fax	: +852-2450 6138
E-mail	: matlab@fugro.com.hk
Website	: www.materialab.com.hk



Ref No.: 100440EN131181

Table 3.2 (Con't)		
Parameters	Action Level	Limit Level
Cadmium in µg/L	≥ 0.5	≥ 0.5
Chromium in µg/L	≥ 1	≥ 1
Aluminium in µg/L	≥ 20	≥ 20

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.

2. For SS and turbidity, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

### Landfill Gas Limit

Depending on the results of the measurements, actions required will be vary and should be set down by the Safety Officer or other appropriately qualified person. The actions shown in Table 3.3 should be referred as the minimum requirements to be encompassed.

Table 3.3 Action Level for Landfill Gas Measurement

Parameter	Measurement	Action
Oxygen	<19 %	<ul> <li>Ventilate to restore oxygen to &gt;19 %</li> </ul>
	<18 %	<ul> <li>Stop works</li> </ul>
		<ul> <li>Evacuate personnel / prohibit entry</li> </ul>
		<ul> <li>Increase ventilation to restore oxygen to &gt;19 %</li> </ul>
Methane	>10 % LEL	<ul> <li>Prohibit hot works</li> </ul>
	(i.e. >0.5 % by volume)	<ul> <li>Ventilate to restore methane to &lt;10 % LEL</li> </ul>
	>20 % LEL	<ul> <li>Stop works</li> </ul>
	(i.e. >1 % by volume)	<ul> <li>Evacuate personnel / prohibit entry</li> </ul>
		<ul> <li>Increase ventilation to restore methane to &lt;10 % LEL</li> </ul>
Carbon	>0.5 %	<ul> <li>Ventilate to restore carbon dioxide to</li> </ul>
dioxide		<0.5 %
	>1.5 %	<ul> <li>Stop works</li> </ul>
		<ul> <li>Evacuate personnel / prohibit entry</li> </ul>
		<ul> <li>Increase ventilation to restore carbon</li> </ul>
		dioxide to <0.5 %

Tuen Mun, N.T.,

Hong Kong.



Ref No.: 100440EN131181

### 4. Construction Phase Environmental Monitoring and Audit

- 4.1 Review of the construction phase environmental monitoring
- 4.1.1 Impact water quality monitoring was performed at three locations with two control stations at Tsang Kok Stream; and two marine locations with one control station in Deep Bay Zone. Piling work was commenced on 21 February 2011 and the foundation piling work was completed on 13 October 2011. The pre-bore piling of the STF was completed on 22 February 2012 and the post monitoring for marine water has been completed on 20 March 2012. Although marine water quality monitoring resumed on 03 July 2012 due to the commencement of pre-bore operation for sheet piling, the pre-bore operation as planned was not carry out. Therefore the impact marine water quality monitoring was suspended on 20 August 2012 and post impact monitoring is not required.

Pursuant to Clause 5.7.1.1 of the EM&A Manual, impact water quality monitoring shall be carried out during site formation, piling and construction of the access road. As the above mentioned site construction has been completed on 17 August 2012 (four weeks post monitoring was commenced by 20 August 2012 and ended on 14 September 2012 inclusively), so that stream water quality monitoring was not required in the reporting period.

Ecology and Visual Impact monitoring were carried out at the East and the Middle Lagoon.

2013				
Monitored Parameters		25 Aug 2013 to 24 Sept 2013	25 Sept 2013 to 24 Oct 2013	25 Oct 2013 to 24 Nov 2013
Stream water	DO, DOS, pH, SS, Temp and Turbidity	Not Required	Not Required	Not Required
Marine water	Cd, Cr and Al	Not Required	Not Required	Not Required
	Avifauna	1	1	1
Ecology	Habitat	2	2	2
	Vegetation	2	2	2
Landscape	Compliance of mitigation measures	2	2	2

Table 4.1Summary of Environmental Monitoring from September 2013 to November2013

4.1.2 Excavation works has been carried out within the WENT landfill consultation zone for the following construction activities during the reporting period: (1) Portion 1 (Landscaping Pond). No gas monitor on 20 September 2013, 01 and 14 October 2013 due to Public Holiday, and 23 September 2013 a.m. due to Typhoon USAGI in the morning.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.

: +852-2450 8233 : +852-2450 6138 Fax E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk



Ref No.: 100440EN131181

#### Table 4.2 Summary of Landfill Gas Monitoring

Tel

Sampling Location	25 Aug 2013 to	25 Sept 2013 to	25 Oct 2013 to
	24 Sept 2013	24 Oct 2013	24 Nov 2013
Portion 1 (Landscaping Pond)	49*#	48*	52

Remark:

#

No landfill gas monitoring on 20 Sept. 01 and 14 Oct 2013 due to public holiday

No landfill gas monitoring on 23 Sept 2013 a.m. due to Typhoon USAGI in the morning

#### 4.2 Synopsis of work undertaken during this quarter

During this quarter in review, construction activity undertaken by the Contractor is listed in Table 4.3.

Construction Activity Undertaken during September 2013 to November 2013 Table 4.3

Month	Construction task item
25 Aug 2013 to	<ul> <li>Waterproofing;</li> </ul>
24 Nov 2013	<ul> <li>Steel Works;</li> </ul>
	<ul> <li>Strut Erection;</li> </ul>
	<ul> <li>Substructure Works: Including Reinforcement, Formwork, Concreting;</li> </ul>
	<ul> <li>Structural Steel Erection;</li> </ul>
	<ul> <li>Roof Installation;</li> </ul>
	<ul> <li>Mechanical Installation;</li> </ul>
	<ul> <li>Façade / Curtain Wall Installation;</li> </ul>
	<ul> <li>E &amp; M Installation;</li> </ul>
	<ul> <li>Inter Decoration;</li> </ul>
	<ul> <li>Glass and Steel Installation;</li> </ul>
	<ul> <li>Condenser Installation;</li> </ul>
	<ul> <li>Lift Installation;</li> </ul>
	<ul> <li>Boundary Wall Installation;</li> </ul>
	<ul> <li>Out-Flow Pipe Installation;</li> </ul>
	<ul> <li>EEC Building Decoration;</li> </ul>
	<ul> <li>Water Pool Work;</li> </ul>
	<ul> <li>Viewing Gallery;</li> </ul>
	<ul> <li>High-voltage Work;</li> </ul>
	Water Pressure Testing;
	<ul> <li>Insulation Works;</li> </ul>
	<ul> <li>High Level Light;</li> </ul>
	Water Features;
	Curtain Wall;
	Office Moving;     Ochie lastellations
	Cable Installation;
	<ul> <li>Switch Board;</li> </ul>
	<ul> <li>Permanent Lighting Installation;</li> <li>T &amp; C Stage at Whele Work Site:</li> </ul>
	<ul> <li>T &amp; C Stage at Whole Work Site;</li> <li>Cordening;</li> </ul>
	<ul> <li>Gardening;</li> <li>Dermanant Baadi and</li> </ul>
	<ul> <li>Permanent Road; and</li> <li>Office Demonization</li> </ul>
	Office Demonization.

4.3 Audit summary of non-compliances of the environmental quality performance limits from 25 August 2013 to 24 November 2013.

### Water Quality

Water quality monitoring was not required in the reporting period.

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Ref No.: 100440EN131181

### Ecology Monitoring

No non-compliance was recorded in the reporting quarter.

Landscape and Visual Monitoring

No non-compliance was recorded in the reporting quarter.

### Landfill Gas Monitoring

Landfill gas monitoring was carried out by a competent person during the excavation, operation in chamber and confined space within the WENT landfill control zone and no non-compliance was recorded in the reporting quarter.

Tel	: +852-2450 8233
Fax	: +852-2450 6138
E-mail	: matlab@fugro.com.hk
Website	: www.materialab.com.hk



Ref No.: 100440EN131181

## 5. Summary of Complaints, Summons and Successful Prosecutions

No documented correspondence regarding complaints, summons and successful prosecutions in association with the construction activities was received in this reporting quarter.

Table 5.1	Summary	of Environmental Complaints and Prosecutions
	Summary	

Complain	ts Logged	Summon	s Served	Successful	Prosecution
Sept 2013 to Nov 2013	Cumulative	Sept 2013 to Nov 2013	Cumulative	Sept 2013 to Nov 2013	Cumulative
0	2	0	0	0	0



Ref No.: 100440EN131181

### 6. Comments and Conclusions for September 2013 to November 2013

### Air Quality

There is no nearby sensitive receiver identified by EIA study hence dust monitoring is not required. The site activities performed in the reporting quarter including vegetation removal, top layer PFA compaction and building works, did not cause significant dust impact. However, the Contractor should deploy necessary dust mitigation measures to reduce potential impacts from construction works to a minimum, which include frequent water spraying at dust generation areas.

### Noise Level

Same as air quality, no sensitive receiver is close to the construction site. In the past three months, no deterioration of the environmental noise level is noted.

After commencement of piling works (even the foundation piling work and pre-bore piling were completed on 13 October 2011 and 22 February 2012 respectively), Contractor should deploy necessary noise mitigation measures to minimize the influence to the wildlife in the Middle Lagoon. Close monitoring of any impact to the habitat will be in place.

### Water Quality

Stream water

Stream water Quality Monitoring was not required in the reporting period.

Marine Water

Marine Water Quality Monitoring was not required in the reporting period.

### Ecology Monitoring

Contractor has followed the mitigation measures to prevent any disturbance to the wildlife in the Middle Lagoon. After commencement of the piling work on 21 February 2011, no significant impact to the wildlife was observed. However, the impact of the construction work will be monitored closely (even the foundation piling work and prebore piling were completed on 13 October 2011 and 22 February 2012 respectively).

Summary of ecology survey is presented in Appendix 2.

### Landscape and Visual Impact Monitoring

In general, the implementation of the proposed measures in construction phase were followed and no non-compliance was observed in the reporting quarter. Summary of observation during the reporting quarter is enclosed in Appendix 3.

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Ref No.: 100440EN131181

### Waste Management Status

C&D Waste	Backfill and excavation works were conducted during the
	reporting period. C&D waste was generated from the current
	activities and sent to public fill.

- General refuse Paper / cardboard, metal and plastics were collected by recycling collectors as far as practicable and general refuse was collected and sent to WENT Landfill.
- Chemical waste 1,400 litres liquid chemical waste was generated during the reporting period and collected by licensed contractor.
- Wastewater Rain water was treated by the silt removal facilities before discharged outside the site. Waste was collected by licensed collector.

Waste flow summary for the previous months is attached in Appendix 4.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Appendix 1

# **Environmental Mitigation Implementation Schedule**

MateriaLab Division,	Tel	: +852-2450 8233
Fugro Development Centre,	Fax	: +852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road,	E-mail	: matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong.	Website	: www.materialab.com.hk



#### **Relevant Legislation Environmental Protection Measures / Mitigation** Implementation Location / Timing **Implementation Stages\*** and Guidelines EIA Ref# Measures Agent С Des 0 Dec Implementation of the Air Pollution Control (Construction Work site / During the S3.8.1 Contractor Air Pollution Control Dust) Regulation and good site practices: construction period (Construction Dust) Regulation Use of regular watering, with complete coverage, to $\sqrt{}$ reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. Use of frequent watering for particularly dusty $\sqrt{}$ construction areas and areas close to ASRs. Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines. $\sqrt{}$ Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. $\sqrt{}$ Tarpaulin covering of all dusty vehicle loads transported • to, from and between site locations. Establishment and use of vehicle wheel and body ٠ V washing facilities at the exit points of the site. $\sqrt{}$ Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods.

### Table 1. Implementation Schedule and Status of Proposed Air Quality Mitigation Measures

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*		Implementation Stades*		Relevant Legislation and Guidelines
				Des	С	0	Dec	
	• Imposition of speed controls for vehicles on unpaved site roads. Ten kilometers per hour is the recommended limit.				$\checkmark$			
	• Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs.				$\checkmark$			
	• Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.				$\checkmark$			

# All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

• Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

• N/A – The associated activities are not in progress during the monitoring month,  $\sqrt{-}$  The proposed mitigation measures is implemented

MateriaLab Division,	Tel	: +852-2450 8233
Fugro Development Centre,	Fax	: +852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road,	E-mail	: matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong.	Website	: www.materialab.com.hk



# Table 2. Implementation Schedule of Proposed Human Health Risk Mitigation Measures

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			Relevant Legislation and Guidelines	
				Des	С	0	Dec	
	Human Health Risk Associated with Radon							
	<ul> <li>Prevention of radon influx from the PFA to the STF buildings</li> <li>A soil cover can be provided beneath the buildings on top of ash lagoon prior to construction works because it reduces the level of radon influx significantly</li> </ul>	STF buildings / During the design, construction and operation of the STF.	Contractor / STF Operator		N/A			EPD's ProPECC Note PN 1/99 Control of Radon Concentration in New Buildings Appendix 2
	<ul> <li>Slab-on-grade can be an option on foundation design</li> <li>Soil suction can also prevent radon from entering the building by drawing the radon from below the building and venting it through a pipe, or pipes, to the air above the building.</li> </ul>				N/A N/A			
	<ul> <li>Provision of Sufficient ventilation of the interior of the STF buildings</li> <li>Forced and natural ventilation should be introduced properly to enhance air exchange rate in the STF buildings.</li> </ul>				N/A			
	<ul> <li>Basement areas should be pressurized by using a fan to blow air into the basement areas from outdoors is suggested. This would create enough pressure at the lowest level indoors to prevent radon from entering into the STF buildings.</li> </ul>				N/A			
	<ul> <li><i>Regular maintenance for the floor slabs and walls</i></li> <li>Cracks and other openings in the foundation should be properly sealed to reduce radon ingress.</li> <li>Sealing the cracks limits the flow of radon into the building thereby making other radon reduction techniques more effective and cost-efficient. It also reduces the loss of conditioned air.</li> </ul>				N/A			

# All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

• Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

• N/A – The associated activities are not in progress during the monitoring month,  $\sqrt{-}$  The proposed mitigation measures is implemented

Page 3 of 20

MateriaLab Division,	Tel	: +852-2450 8233
Fugro Development Centre,	Fax	: +852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road,	E-mail	: matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong.	Website	: www.materialab.com.hk

# MateriaLab

# Table 3. Implementation Schedule of Proposed Waste Management Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			Relevant Legislation and Guidelines	
				Des	С	0	Dec	
\$5.5.1	<i>Good Site Practices</i> Recommendations for good site practices during the construction activities include:	Work site / During the construction period	Contractor					Waste Disposal Ordinance (Cap.354)
	• Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site				$\checkmark$			ETWB TCW No. 19/2005
	• Training of site personnel in proper waste management and chemical handling procedures				$\checkmark$			
	• Provision of sufficient waste disposal points and regular collection of waste							
	• Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers							
	• Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.							
\$5.5.1	Waste Reduction Measures	Work site / During planning & design	Contractor		,			
	• Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:	stage, and construction stage			N			

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing Implementation Agent			Implementation Stages*			Relevant Legislation and Guidelines
				Des	С	0	Dec	
	• The design of the foundation works should minimize the amount of excavated material to be generated.				$\checkmark$			
	• Excavated soil should be reused on site as far as possible, e.g. for landscape works, in order to minimize the amount of public fill to be disposed off-site.				$\checkmark$			
	• Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.				√			
	• Encourage collection of aluminium cans by individual collectors by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the work force				V			
	• Proper storage and site practices to minimize the potential for damage or contamination of construction materials.							
	• Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste.				V			
\$5.5.1	General Refuse General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.	Work site / During the construction period	Contractor		V			Public Health and Municipal Services Ordinance (Cap. 132)

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	Implei	nentat	iges*	Relevant	
EIA Ref #			Agent	Des	C	0	Dec	Legislation and Guidelines
S5.5.1	Construction and Demolition Material							
	In order to minimize the impact resulting from collection and transportation of C&D material for off-site disposal, the excavated material arising from site formation and foundation works should be reused on-site as backfilling material and for landscaping works as far as practicable. Other mitigation requirements are listed below:	Work site / During design stage & construction period	Contractor	N	N			ETWB TCW No. 33/2002 ETWB TCW No. 19/2005 ETWB TCW No. 31/2004
	• A Waste Management Plan, which becomes part of the Environmental Management Plan, should be prepared in accordance with ETWB TCW No.19/2005.				$\checkmark$			
	• A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be proposed.				$\checkmark$			
	• In order to monitor the disposal of C&D material at public filling facilities and landfills and to control fly-tipping, a trip-ticket system should be included. One may make reference to ETWB TCW No. 31/2004 for details.				$\checkmark$			
S5.5.1	Chemical Waste							
	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible	Work site / During the construction period	Contractor		V			Waste Disposal (Chemical Waste)(General) Regulation)

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*		ges*	Relevant Legislation and	
			0	Des	С	0	Dec	Guidelines
	chemicals should be stored separately. Appropriate labels should							
	be securely attached on each chemical waste container indicating							
	the corresponding chemical characteristics of the chemical waste,							
	such as explosive, flammable, oxidizing, irritant, toxic, harmful,							
	corrosive, etc. The Contractor shall use a licensed collector to							
	transport and dispose of the chemical wastes, to either the							
	Chemical Waste Treatment Centre at Tsing Yi, or another							
	licensed facility, in accordance with the Waste Disposal							
	(Chemical Waste) (General) Regulation.							

# All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

• Des – Design, C – Construction, O – Operation, and Dec – Decommissioning

• N/A – The associated activities are not in progress during the monitoring month,  $\sqrt{}$  - The proposed mitigation measures is implemented

MateriaLab Division,	Tel	: +852-2450 8233
Fugro Development Centre,	Fax	: +852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road,	E-mail	: matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong.	Website	: www.materialab.com.hk

# MateriaLab

# Table 4. Implementation Schedule of Proposed Land Contamination Preventive Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Imple	mentat	nges*	Relevant Legislation and Guidelines	
				Des	С	0	Dec	
\$5.6.3	<ul> <li>Fuel Oil Tank Construction and Test</li> <li>The fuel tank to be installed should be of specified durability</li> <li>Double skin tanks are preferable</li> <li>Underground fuel storage tank to be installed should be placed within a concrete pit</li> <li>The concrete pit shall be accessible to allow regular tank integrity tests to be carried out at regular intervals</li> <li>The tank integrity tests should be conducted by an independent qualified surveyor or structural engineer</li> <li>Any potential problems identified in the test should be</li> </ul>		Contractor/ STF Operator	V	$\frac{1}{\sqrt{N/A}}$			
\$5.6.3	<ul> <li>rectified as soon as possible</li> <li>Fuel Oil Pipeline Construction and Test</li> <li>Installation of aboveground fuel oil pipelines is preferable; if underground pipelines are unavoidable, concrete lined trenches should be constructed to contain the pipelines</li> <li>Double skin pipelines are preferable</li> <li>Distance between the fuel oil refuelling points and the fuel oil storage tank shall be minimized</li> <li>The integrity tests for the pipelines should be conducted by an independent qualified surveyor or structural engineer at regular intervals</li> <li>Any potential problems identified in the test should be rectified as soon as possible</li> </ul>	Fuel Oil Pipelines/ Design, Construction and Operation Phase	Contractor/ STF Operator	V				
S5.6.3	<ul> <li>Fuel Oil Leakage Detection</li> <li>Installation of leak detection device at storage tank and pipelines</li> </ul>	Fuel Oil Storage Tank	Contractor/ STF Operator	N/A	N/A			

# All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

• Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

• N/A – The associated activities are not in progress during the monitoring month,  $\sqrt{-}$  The proposed mitigation measures is implemented

MateriaLab Division,	Tel	: +852-2450 8233
Fugro Development Centre,	Fax	: +852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road,	E-mail	: matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong.	Website	: www.materialab.com.hk

# MateriaLab

### Table 5. Implementation Schedule of Proposed Water Pollution Control Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			iges*	Relevant Legislation and Guidelines
				Des	С	0	Dec	und Guidelines
\$6.7.2	<ul> <li>Construction Runoff and Drainage</li> <li>Site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" shall be followed as far as practicable in order to minimize surface runoff and the chance of erosion:</li> <li>At the start of site establishment, internal drainage works and erosion and sedimentation control facilities shall be implemented. Channels, earth bunds or sand bag barriers shall be provided on site to direct stormwater to silt removal facilities. The detailed design and installation of the temporary on-site drainage system shall be undertaken by the contractor prior to the commencement of construction.</li> <li>Before commencing any site formation work, all sewer and drainage connections shall be sealed to prevent debris, soil, sand etc. from entering public sewers/drains.</li> <li>Boundaries of earthworks shall be surrounded by dykes or embankments for flood protection, as necessary.</li> <li>Sand/silt removal facilities such as sand traps, silt traps and sediment basins shall be provided to remove sand/silt particles from runoff to meet the standards of the Technical</li> </ul>	Work site / During the construction period	Contractor		$\sqrt{N/A}$ $\sqrt{\sqrt{V}}$			ProPECC PN 1/94; WPCO

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Imple	mentat	ion Sta	ıges*	Relevant Legislation and Guidelines
				Des	С	0	Dec	and Guidennes
	<ul> <li>Memorandum under the Water Pollution Control Ordinance. The design of silt removal facilities shall be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures shall be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms.</li> <li>Water pumped out from foundation piles shall be discharged into silt removal facilities.</li> <li>During rainstorms, exposed slope/soil surfaces shall be covered by a tarpaulin or other means, as far as practicable. Other measures that need to be implemented before, during and after rainstorms are summarized in ProPECC PN 1/94.</li> <li>Exposed soil areas shall be minimized to reduce potential for increased siltation and contamination of runoff.</li> <li>Earthwork final surfaces shall be well compacted and subsequent permanent work or surface protection shall be immediately performed. Open stockpiles of construction materials or construction wastes on- site of more than 50m3 shall be covered with tarpaulin or similar fabric during rainstorms.</li> </ul>			Des	$\mathbf{C}$ N/A 	0	Dec	
	• All vehicles shall be cleaned before leaving the works area to ensure no earth, mud and debris is deposited on roads. An adequately designed and				V			

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



	Environmental Protection Measures / Mitigation Measures	Lessting / Timing	Implementation Agent	Imple	mentat	ion Sta	Delevent Logislation	
EIA Ref #		Location / Timing	Implementation Agent	Des	C	0	Dec	Relevant Legislation and Guidelines
	sited wheel washing bay shall be provided at every site exit. The wheel washing facility shall be designed to minimize the intake of surface water (rainwater). Wash-water shall have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process.							
S6.7.2	<ul> <li>General Construction Activities</li> <li>Debris and refuse generated on-site shall be collected, handled and disposed of properly to avoid entering the nearby water bodies and public drainage system. Stockpiles of cement and other construction materials shall be kept covered when not being used.</li> <li>Oils and fuels shall only be used and stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to nearby water bodies and public drains, all fuel tanks and storage areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund shall be drained of rainwater after a rain event.</li> </ul>	Work site / During the construction period	Contractor					ProPECC PN 1/94;
\$6.7.2	<ul> <li>Sewage Effluents</li> <li>Temporary sanitary facilities, such as portable chemical toilets, shall be employed on-site where necessary to handle sewage from the workforce. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities.</li> </ul>	Work site / During the construction period	Contractor		V			ProPECC PN 1/94; WPCO

MateriaLab Division,	Tel	: +852-2450 8233
Fugro Development Centre,	Fax	: +852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road,	E-mail	: matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong.	Website	: www.materialab.com.hk



	Environmental Protection Measures / Mitigation	Location / Timing Im	Implementation Agent	Imple	mentati	ion Sta	Relevant Legislation	
EIA Ref #	Measures	Location / Timing	Implementation Agent	Des	С	0	Dec	and Guidelines
S6.7.2	Release of PFA Leachate from Ash Lagoon into the Aquatic Environment	Deep Bay	Contractor					WPCO
	• Environmental monitoring and audit (EM&A) should be included to ensure that the foundation construction would not cause an unacceptable release of PFA leachate into the Deep Bay waters. The parameters to be measured should include the heavy metals such as cadmium, chromium and aluminium, which have the greatest tendency to leach from the lagooned PFA into the seawater. Details of the measurement requirements are presented in the EM&A manual	the construction period			$\checkmark$			

# All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and/or accepted public comment to the proposed project.

• Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

• N/A – The associated activities are not in progress during the monitoring month,  $\sqrt{-}$  The proposed mitigation measures is implemented

MateriaLab Division,	Tel
Fugro Development Centre,	Fax
5 Lok Yi Street, 17 M.S. Castle Peak Road,	E-mail
Tai Lam, Tuen Mun, N.T., Hong Kong.	Website

: +852-2450 8233 : +852-2450 6138 il : matlab@fugro.com.hk ite : www.materialab.com.hk

# **MateriaLab**

## Table 6. Implementation Schedule of Proposed Ecological Mitigation Measures

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			ıges*	Relevant Legislation and Guidelines
				Des	С	0	Dec	
S7.8.2	Measures to Minimize Disturbance Impact to Wildlife							
	• Hoarding of 3m high shall be set up along the boundary of the works areas and associated site access to shield the fauna and breeding population of Little Grebe in the Middle Lagoon from the disturbance impact of machinery.	Boundary of works areas/ Construction Phase	Contractor		$\checkmark$			
	• The works boundaries shall not go beyond the proposed Project Area. All work crews, equipment and human activities shall be confined within the designated works area only. No personnel should encroach or wilfully disturb any wild animals and their habitats. Traffic and human access from the western side of the Project Area should be avoided.	Boundary of works areas/ Construction Phase	Contractor		V			
	• Fencing with climbers or plantation shall be provided, where appropriate, along the STF site boundary and the two sides of access road to screen the surrounding habitats from the STF works areas.	Boundary of works areas/ Operation Phase	Contractor		$\checkmark$			

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



EIA Ref #	Environmental Protection Measures / Mitigation Measures		Implementation Agent	Imple	ementat	ion Sta	Relevant Legislation and Guidelines	
				Des	С	0	Dec	
S7.8.2	Measures to Minimize Impact to natural habitats							
	• Where practicable, all proposed works shall be conducted in existing built up area to minimize impact to natural habitats.	Works areas/ Design and Construction Phase	STF Designer/ Contractor	V	$\checkmark$			
	• The abutment (permanent structure) for the vehicular bridge shall avoid streambed. The number and size of the temporary supporting structures to be installed over the streambed during construction shall be minimized as far as practicable.	Vehicular bridge/ Design and Construction Phase	STF Designer/ Contractor	$\checkmark$	V			ETWB TC (Works)
	<ul> <li>The temporarily affected natural habitats, including streambed, shall be reinstated after the completion of works.</li> <li>For affected natural stream section, placement of substrates of similar size and composition to those of original streambed shall be considered to encourage colonization.</li> </ul>	Works Area/ Operation Phase Works Area/ Operation Phase	Contractor Contractor		N/A N/A			No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works
\$7.8.2	<ul> <li>Minimise sedimentation/water quality impacts to waterbodies</li> <li>Measures to control potential sedimentation/ water quality impacts during the construction phase shall be implemented.</li> <li>T o minimize the potential water quality impacts from the construction works located at any river channels, natural streams or seafront, the practices outlined in</li> </ul>	Whole Site/ Construction Phase	Contractor		N N			ETWB TC (Works) No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

 Tel
 :+852-2450 8233

 Fax
 :+852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk

# **MateriaLab**

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing Implementation Agent				ion Sta	Relevant Legislation and Guidelines	
				Des	С	0	Dec	
	ETWB TC (Works) No. 5/2005 "Protection of natural streams/rivers from adverse impacts arising from construction works" shall be adopted where applicable.							
87.8.2	<ul> <li>Minimize noise disturbance</li> <li>Noise mitigation measures including the use of quieter piling machinery and construction plants shall be implemented to lower the noise level due to construction works.</li> <li>Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction programme.</li> <li>Machines and plant which may be in intermittent use shall be shut down to a minimum.</li> <li>Plant known to emit noise strongly in one direction, shall be oriented so that the noise is directed away from the Middle Lagoon, where possible.</li> <li>Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction period.</li> <li>Mobile plant (such as generator) shall be sited as far away from the Middle Lagoon as possible.</li> <li>Material stockpiles and other structures shall be effectively utilized, where practicable, to screen noise from on-site construction activities.</li> </ul>	Whole Site/ Construction Phase	Contractor		$\begin{array}{c} \sqrt{}\\ \phantom{0$			ETWB TC (Works) No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works

MateriaLab Division,
Fugro Development Centre,
5 Lok Yi Street, 17 M.S. Castle Peak Road,
Tai Lam, Tuen Mun, N.T., Hong Kong.

 Tel
 :+852-2450 8233

 Fax
 :+852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk

# MateriaLab

EIA Ref #	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Imple	mentat	ion Sta	ages*	Relevant Legislation and Guidelines
				Des	С	0	Dec	
S7.8.3	<ul> <li>Measures to Mitigate the Loss of Vegetation</li> <li>All vegetation located within the work areas shall be preserved as far as practicable.</li> <li>To compensate for the loss of the vegetation and habitats, tree planting shall be provided in the site area where possible. Species chosen for planting shall be similar to the species identified in the survey and be native to Hong Kong or the Southern China.</li> </ul>	Whole Site / Design, Construction and Operation Phase	Contractor / STF Operator	V	√ √			
S7.8.4	<ul> <li>Enhancement Measures to Create Additional Habitat for Little Grebe</li> <li>An additional habitat for Little Grebe shall be created in a less disturbed area located at the northeastern part of the proposed STF.</li> <li>The created habitat shall be provided in form of shallow pond(s) incorporating suitable habitat characteristics for Little Grebe. The water level of the created pond shall be kept between 1.5 m to 2 m.</li> <li>Emergent vegetation shall be planted and fish population shall be controlled to allow development of aquatic invertebrate populations as prey of Little Grebe.</li> <li>To screen the created habitat from disturbance due to nearby landfill traffic, planting of native plants shall be provided on the boundary of the pond(s) as appropriate.</li> <li>Prior to construction of the pond(s), detailed Habitat Creation and Management Plan (HCMP) of the created habitat prepared by experienced ecologist(s) with over seven year experience in relevant field shall be circulated to relevant departments including AFCD</li> </ul>	Within Project Area/ Design Phase, Construction and Operation Phase	Contractor / STF Operator	~	N/A N/A N/A N/A			

# All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

• Des - Design, C - Construction, O - Operation and Dec – Decommissioning

• N/A – The associated activities are not in progress during the monitoring month,  $\sqrt{-}$  The proposed mitigation measures is implemented

MateriaLab Division,	Tel	: +852-2450 8233
Fugro Development Centre,	Fax	: +852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road,	E-mail	: matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong.	Website	: www.materialab.com.hk

# **MateriaLab**

# Table 7. Implementation Schedule for Landscape and Visual Impact

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			Relevant Legislation and Guidelines	
				Des	С	0	Dec	
T able 9.4 CM-01	<u>Contaminant/ Sediment Control</u> – Suitable temporary barriers, covers and drainage provisions shall be provided around construction works to avoid discharge of contaminants (such as bleeding from in-situ concrete works) and sediments into sensitive water-based habitats, especially the tidal streams and the mangrove.	Work site / During the construction period	Contractor		V			
T able 9.4 CM-02	Early Planting of Tall Trees – Tall trees proposed under mitigation measure OM-02 shall be planted early, providing visual effect also during construction.	Work site / During the construction period	Contractor		N/A			
T able 9.4 CM-03	<u>Good Site Practice</u> – Construction activities should be restricted to works areas and should be clearly demarcated onsite. Piling of construction materials onsite shall be carefully considered for possible impacts before carrying out.	Work site / During the construction period	Contractor		V			
T able 9.4 CM-04	<u>Existing Trees within Works Areas</u> – All existing trees within work sites shall be properly maintained and protected for their crowns, trunks and roots.	Work site / During the construction period	Contractor	V	V			
T able 9.4 OM-01	<u>Sensitive Bridge Design</u> – The bridge of the proposed access road shall be sensitively designed to minimize impact to the tidal stream and mangrove. It shall be constructed with minimal use of in-situ concreting and with maximum use of precast or prefabricated elements. No pile or support shall be erected within the stream channel.	Bridge of access road / During the design & construction phases	Contractor	V	N/A			

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Imple	ementat	ion Sta	Relevant Legislation and Guidelines	
				Des	С	0	Dec	
T able 9.4 OM-02	<u>Tall trees for Chimney</u> – Fast-growing tall trees shall be planted along the east side of the ash-lagoon to counterbalance possible exotic silhouettes, such as from the chimney, of the proposed sludge treatment facilities for sensitive viewers in Pak Nai. The trees shall be planted during the early stage of the construction to ensure effectiveness during operation. They will also help to lessen the visual impact during construction, as already suggested in mitigation measure CM-02.	East side of ash lagoon / During the design & construction phases	Contractor	V	N/A			
Table 9.4 OM-03	<u>Suitable Reinstatement at Ash-lagoon</u> – Affected perimeter of the proposed works area within the ash- lagoon shall be reinstated with suitable planting materials. Traditional reinstatement planting approach for construction projects may not work well for this project. Certain existing grasses and small shrubs have self-seeded the ash- lagoon, demonstrating their tolerance to salts, alkalinity and possible trace metals in the ash. Therefore the same or similar species of vegetation shall be used.	Perimeter of works area / During the design & construction phases	Contractor	V	N/A			
Table 9.4 OM-04	<u>Existing Tree Transplanting</u> – The proposed access roadworks may affect few existing trees, which shall be transplanted as far as practical. A comprehensive tree survey is recommended to locate these trees.	Access road / During the design & operation phases	Contractor	V	N/A			
Table 9.4 OM-05	<u>Planting at Road Intersection</u> – Suitable planting of woodland trees and shrubs shall be provided for the proposed access roadworks at the junction with Nim Wan Road.	Junction of access road with Nim Wan Road / During the design & operation phases	Contractor	V	N/A			

# All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

• Des - Design, C - Construction, O - Operation and Dec – Decommissioning

• N/A – The associated activities are not in progress during the monitoring month,  $\sqrt{-}$  The proposed mitigation measures is implemented

MateriaLab Division,	Tel	: +852-2450 8233
Fugro Development Centre,	Fax	: +852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road,	E-mail	: matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong.	Website	: www.materialab.com.hk

# **MateriaLab**

# Table 8. Implementation Schedule of Proposed Landfill Gas Hazard Protection Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing Implementation Agent			ementat	ion Sta	Relevant Legislation and Guidelines	
				Des	С	0	Dec	
S10.7.2	Appointment of Safety Officer Appoint a properly trained safety officer and provide with appropriate equipment to measure and monitor LFG hazard.	Work Site / During the construction phase	Contractor		$\checkmark$			
\$10.7.2	<b>Safety Measures - Excavation</b> Staff should receive appropriate training on working in areas susceptible to landfill gas, fire and explosion hazards. Excavation procedures and code of practice should be implemented.	Work Site / During the construction phase	Contractor		$\checkmark$			
S10.7.2	<u>Safety Measures – Welding, Flame-Cutting and Hot works</u> Hot works should be confined to open areas away from any trench or excavation. Should hot works must be carried out in trenches or confined space, "permit to work" procedures should be followed.	Work Site / During the construction phase	Contractor		$\checkmark$			
\$10.7.2	<b>Safety Measures – Enclosed Spaces</b> Site offices or buildings located within WENT Landfill Consultation Zone which have the capacity to accumulate landfill gas, then they should either be located in an area which has been proven to be free of landfill gas; or be raised clear of the ground by a minimum of 500mm.	Enclosed Spaces within WENT Consultant Zone / During the construction phase	Contractor		N/A			
S10.7.2	<b>Safety Measures – Electrical Equipment</b> Any electrical equipment, such as motors and extension cords, should be intrinsically safe.	Work Site / During the construction phase	Contractor		N/A			

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



EIA Ref#	Environmental Protection Measures / Mitigation Measures	tal Protection Measures / Mitigation Location / Timing	Implementation Agent	Imple	mentat	ion Sta	Relevant Legislation and Guidelines	
				Des	С	0	Dec	
\$10.7.2	<b>Safety Measures – Piping</b> During piping assembly or conduiting construction, all valves/seals should be closed immediately after installation. As construction progresses, all valves/seals should be closed as installed to prevent the migration of gases through the pipeline/conduit. All piping/conduiting should be capped at the end of each working day.	Work Site / During the construction phase	Contractor		N/A			
S10.7.2	<b>Safety Measures – Fire Safety</b> Adequate fire safety equipments should be provided on site. Workers and visitors should be notified of the potential fire hazards. Safety notices should be posted around the site warning the anger and potential hazards.	Work Site / During the construction phase	Contractor		$\checkmark$			
810.7.2	Safety Measures – Confined Spaces Precautionary measures should include ensuring that staff members are aware of the potential hazards of working in confined spaces, and that appropriate monitoring procedures are in place to prevent hazards in confined spaces.	Confined Spaces at Work Site / During the construction phase	Contractor		N/A			
\$10.7.2	<b>Monitoring</b> Periodically during ground-works within the Consultation Zone, the works area should be monitored for methane, carbon dioxide and oxygen using appropriately calibrated portable gas detection equipment. The monitoring frequency and areas to be monitored shall be set down prior to commencement of ground-works. Depending on the results of the measurements, actions required will vary. As a minimum these should encompass those actions specified in Table 10.6 of the EIA Report.	Work Site / During the construction phase	Contractor		N/A			

# All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

• Des - Design, C - Construction, O - Operation and Dec – Decommissioning

• N/A – The associated activities are not in progress during the monitoring month,  $\sqrt{-}$  The proposed mitigation measures is implemented

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Appendix 2

## **Summary of Ecology Monitoring**

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Ref No.: 100440EN131181

		25 Au 24 S	g 2013 to ept 2013	25 Se 24 C	pt 2013 to Oct 2013		ct 2013 to lov 2013
Species Name	Scientific Name	Middle	Notable /	Middle	Notable /	Middle	Notable /
		Lagoon	Breeding Activity	Lagoon	Breeding Activity	Lagoon	Breeding Activity
Barn Swallow	Hirundo rustica	60	None observed	0	-	0	-
Black Drongo	Dicrurus macrocercus	1	None observed	0	-	0	-
Black-faced Bunting	Emberiza spodocephala	0	-	0	-	2	None observed
Black Kite	Milvus migrans	0	-	2	None observed	0	-
Black-winged Stilt	Himantopus himantopus	37	None observed	0	-	0	-
Brown Shrike	Lanius cristatus	1	None observed	0	-	0	-
Chestnut Bulbul	Hemixos castanonotus	0	-	0	-	2	None observed
Chinese Bulbul	Pycnonotus sinensis	35	Including juveniles	2	None observed	14	None observed
Chinese Pond Heron	Ardeola bacchus	1	None observed	0	-	0	-
Common Greenshank	Tringa nebulosa	3	None observed	6	None observed	0	-
Common Kinfisher	Alcedo atthis	1	None observed	0	-	0	-
Common Moorhen	Gallinula chloropus	2	Both juveniles	0	-	0	-
Common Sandpiper	Actitis hypoleucos	1	None observed	0	-	0	-
Common Starling	Sturnus vulgaris	0	-	1	None observed	0	-
Crested Myna	Acridotheres cristatellus	34	None observed	34	None observed	8	None observed
Daurian Redstart	Phoenicurus auroreus	0	-	0	-	5	None observed
Dusky Warbler	Phylloscopus fuscatus	0	-	0	-	10	None observed
Eastern Yellow Wagtail	Motacilla tschutschensis	80	None observed	12	None observed	0	-
Euarian Hoopoe	Upupa epops	1	None observed	0	-	0	-
Eurasian Skylark	Alauda arvensis	0	-	5	None observed	0	-
Green Sandpiper	Tringa ochropus	2	None observed	2	None observed	0	-
Hair-crested Drongo	Dicrurus hottentottus	0	-	1	None observed	0	-
Japanese Sparrowhawk	Accipiter gularis	0	-	1	None observed	0	-
Japanese White- eye	Zosterops japonica	30	None observed	0	-	0	-
Little Bunting	Emberiza pusilla	0	-	0	-	8	None observed
Little Egret	Egretta garzetta	15	None observed	5	None observed	0	-
Little Grebe	Tachybaptus ruficolis	72	Adults and large immatures	0	-	0	-
Little Ringed Plover	Charadrius dubius	2	None observed	57	None observed	0	-
Little Swift	Apus affinis	5	None observed	0	-	0	-
Long-tailed Shrike	Lanius schach	2	None observed	0	-	1	None observed
Long-toed Stint	Calidris subminuta	4	None observed	0	-	0	-

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Ref No.: 100440EN131181

(C	on	't)
$\sim$	011	· · /

		24 Se	g 2013 to pt 2013	24 Óc	t 2013 to et 2013	24 No	t 2013 to ov 2013
Species Name	Scientific Name	Middle Lagoon	Notable / Breeding Activity	Middle Lagoon	Notable / Breeding Activity	Middle Lagoon	Notable / Breeding Activity
Marsh Sandpiper	Tringa stagnatilis	2	None observed	0	-	0	-
Masked Laughingthrush	Garrulax perspicillatus	0	-	0	-	1	None observed
Olive-backed Pipit	Anthus hodgsoni	0	-	0	-	2	None observed
Oriental Magpie Robin	Copsychus saularis	1	Juvenile	1	None observed	0	-
Oriental Reed Warbler	Acrocephalus orientalis	5	None observed	0	-	0	-
Pied Kingfisher	Ceryle rudis	1	None observed	0	-	0	-
Plain Prinia	Prinia inornata	15	Singing	0	-	2	None observed
Plaintive Cuckoo	Cacomantis merulinus	1	None observed	0	-	0	-
Red-billed Starling	Spodiospar sericeus	0	-	0	-	20	None observed
Red-throated Pipit	Anthus cervinus	0	-	2	None observed	0	-
Red Turtle Dove	Streptopelia tranquebarica	1	None observed	0	-	0	-
Scaly-breasted Munia	Lonchura punctulata	15	None observed	4	None observed	16	None observed
Spotted Dove	Spilopelia chinensis	3	None observed	2	None observed	19	None observed
Stejneger's Stonechat	Saxicola torquatus	0	-	2	None observed	0	-
White-shouldered Starling	Sturnus sinensis	37	None observed	0	-	0	-
White-throated Kingfisher	Halcyon smyrensis	2	None observed	1	None observed	0	-
White Wagtail	Motacilla alba	15	None observed	84	None observed	6	None observed
Yellow-bellied Prinia	Prinia flaviventris	3	None observed	2	None observed	1	None observed
Yellow-browed Warbler	Phylloscopus inorntus	0	-	1	None observed	2	None observed
Total Numbers		490		227		199	
Total Species		34		21		17	

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Appendix 3

## Summary of Landscape and Visual Impact Survey

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Ref No.: 100440EN131181

				2013 to ot 2013		t 2013 to ct 2013	25 Oct 2013 to 24 Nov 2013				
ID No.	Nature / Type	Landscape and Visual Mitigation Measures	Status	Remarks	Status	Remarks	Status	Remarks			
CM 1	Design / Construction Planning	Topsoil, where identified, should be stripped and stored for re- use in the construction of the soft landscape works, where practical.	Not applicable.	Suitable topsoil already imported for planting during landscape planting phase. As per observation on site, the PFA excavated out due to site formation work had been under treatment (dehydration), and is backfilled to its original location inside the site boundary. Capping of the PFA is established to prevent spreading in air. Photographic record of top soil imported has been shown in Table 4.5. Monthly EM&A Report of Sept 2013.	Not applicable.	Suitable topsoil already imported for planting during landscape planting phase. As per observation on site, the PFA excavated out due to site formation work had been under treatment (dehydration), and is backfilled to its original location inside the site boundary. Capping of the PFA is established to prevent spreading in air. Photographic record of top soil imported has been shown in Table 4.5. Monthly EM&A Report of Oct 2013.	Not applicable.	Suitable topsoil already imported for planting during landscape planting phase. As per observation on site, the PFA excavated out due to site formation work had been under treatment (dehydration), and is backfilled to its original location inside the site boundary. Capping of the PFA is established to prevent spreading in air. Photographic record of topsoil imported has been shown in Table 4.5. Monthly EM&A Report of Nov 2013.			
CM 2	Site Practice	Existing trees to be retained on site should be carefully protected during construction.	The contractor has confirmed T758 to be retained on site and proper tree protection would be required for T758. Amendment to the tree felling application already updated and sent to DLO on 17 July 2013.	Photographic record of the retained tree T758 is shown in Table 4.5. Monthly EM&A Report of Sept 2013.	The contractor has confirmed T758 to be retained on site and proper tree protection would be required for T758. Amendment to the tree felling application already updated and sent to DLO on 17 July 2013.	Photographic record of the retained tree T758 is shown in Table 4.5. Monthly EM&A Report of Oct 2013.	The contractor has confirmed T758 to be retained on site and proper tree protection would be required for T758. Amendment to the tree felling application already updated and sent to DLO on 17 July 2013.	Photographic record of the retained tree T758 is shown in Table 4.5. Monthly EM&A Report of Nov 2013.			
CM 3	Design / Construction Planning	Trees unavoidably affected by the works should be transplanted where practical.	Transplant trees awaiting area to be transplanted back to site.	Transplant tree number T332/337/338/3 46/335 have been transplanted to site.	Transplant trees awaiting area to be transplanted back to site.	Remaining Transplant tree number T334/347/348/3 49/351/ 352/353/358 have been transplanted to site. Conditions of the transplanted trees under close monitoring.	Total 13 nos. of transplant trees have been transplanted back to the site.	Conditions of the transplanted trees under close monitoring.			

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Ref No.: 100440EN131181

	ID Nature / No. Type CM Design / Construction Planning CM Site Practice			2013 to ot 2013		t 2013 to tt 2013	25 Oct 2013 to 24 Nov 2013				
ID No.		Landscape and Visual Mitigation Measures	Status	Remarks	Status	Remarks	Status	Remarks			
CM 4	Nature / Type         Landscape and Visual Mitigation         Status           Design / Construction Planning         Compensatory should be provided to compensate for felled trees.         New trees planting is proposed on 1 either side of the bridge at profino 6 to fu the EIA requirements. Trees planting programme already submitted by soft landscap	planting is proposed on the either side of the bridge at portion 6 to fulfill the EIA requirements. Trees planting programme already	Location for the compensatory trees to be verified on site by the contractor and shown in Table 4.5. Monthly EM&A Report of Sept 2013.	New trees planting is proposed on the either side of the bridge at portion 6 to fulfill the EIA requirements. Trees planting programme already submitted by soft landscape contractor Bluet.	First batch of compensatory trees has commenced and shown in Table 4.5. Monthly EM&A Report of Oct 2013.	First batch of compensatory trees has finished. Site photos refer to Table 4.5. Monthly EM&A Report of Nov 2013.					
CM 5	Site Practice			Night-time work was implemented from 7pm to 6am for certain period in September 2013. The lighting is confined to the construction site without affecting the periphery area. Photographic record of the night-time working is shown in Table 4.5. Monthly EM&A Report of Sept 2013.	In progress.	Night-time work was implemented from 7pm to 6am for certain period in October 2013. The lighting is confined to the construction site without affecting the periphery area. Photographic record of the night-time working is shown in Table 4.5. Monthly EM&A Report of Oct 2013.	In progress.	Night-time work was implemented from 7pm to 6am for certain period in November 2013. The lighting is confined to the construction site without affecting the periphery area. Photographic record of the night-time working is shown in Table 4.5. Monthly EM&A Report of Nov 2013.			
CM 6	Construction	decorative screen hoarding compatible with the surrounding	Completed.	Erection of decorative screen hoarding has been set up along the site boundary.	Completed.	Erection of decorative screen hoarding has been set up along the site boundary.	Completed.	Erection of decorative screen hoarding has been set up along the site boundary.			

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Appendix 4

**Summary of Waste Flow** 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Ref No.: 100440EN131181

#### **Summary of Waste Flow**

Type of Waste	Quantity Generated in Sept 2013	Quantity Generated in Oct 2013	Quantity Generated in Nov 2013
Inert C&D Waste*	191.589m <sup>3</sup>	172.974m <sup>3</sup>	67.932m <sup>3</sup>
Chemical Waste (Liquid)	NIL	NIL	1,400.000 L
Chemical Waste (Solid)	NIL	NIL	NIL
Metal	10,650.000kg	17,755.000kg	13,510.000kg
Paper / Cardboard Packaging	1,807.000kg	1,523.000kg	3,707.000kg
Plastic	15.000kg	40.000kg	NIL
Others, e.g. General Refuse	152.775m <sup>3</sup>	144.406m <sup>3</sup>	115.481m <sup>3</sup>

Remarks: Density of Inert C&D waste and general refuse is 1.9 tonne/m<sup>3</sup> and 1.6 tonne/m<sup>3</sup> respectively \* The total quantity generated of Insert C&D Waste in April and May 2012 were revised as the quantities of reused in other projects need to be included.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Appendix 5

**Event / Action Plan for Water Quality** 

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone Telefax E-mail Website

: +852-2450 8233 : +852-2450 6138 : matlab@fugro.com.hk : www.fugro.com



#### **Event/Action Plan for Water Quality**

Event	ET Leader	IEC	SOR	Contractor
Action level being exceeded by one sampling day	<ul> <li>Repeat <i>in situ</i> measurement to confirm findings;</li> <li>Identify reasons for non-compliance and source(s) of impact;</li> <li>Inform IEC and Contractor;</li> <li>Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>Discuss mitigation measures with IEC and Contractor;</li> <li>Repeat measurement on next day of exceedance.</li> </ul>	<ul> <li>Discuss with ET and Contractor on the mitigation measures;</li> <li>Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly;</li> <li>Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul> <li>Discuss with IEC on the proposed mitigation measures;</li> <li>Make agreement on the mitigation measures to be implemented.</li> <li>Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul> <li>Inform the SOR and confirm notification of the non- compliance in writing;</li> <li>Rectify unacceptable practice;</li> <li>Check all plant and equipment;</li> <li>Consider changes of working methods;</li> <li>Discuss with ET and IEC and propose mitigation measures to IEC and SOR;</li> <li>Implement the agreed mitigation measures.</li> </ul>
Action level being exceeded by more than one consecutive sampling day	<ul> <li>Repeat in situ measurement to confirm findings;</li> <li>Identify reasons for non- compliance and source(s) of impact;</li> <li>Inform IEC and Contractor;</li> <li>Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>Discuss mitigation measures with IEC and Contractor;</li> </ul>	<ul> <li>Discuss with ET and Contractor on the mitigation measures;</li> <li>Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly;</li> <li>Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul> <li>Discuss with IEC on the Proposed mitigation measures;</li> <li>Make agreement on the mitigation measures to be implemented;</li> <li>Assess the effectiveness of the implemented mitigation measures.</li> </ul>	<ul> <li>Inform the SOR and confirm notification of the non- compliance in writing;</li> <li>Rectify unacceptable practice;</li> <li>Check all plant and equipment; Consider changes of working methods;</li> <li>Discuss with ET and IEC and propose mitigation measures to IEC and SOR within three working days;</li> </ul>

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone	
Telefax	
E-mail	
Website	

: +852-2450 8233 : +852-2450 6138 : matlab@fugro.com.hk : www.fugro.com



Event	ET Leader	IEC	SOR	Contractor
Limit level being exceeded by one	<ul> <li>Ensure mitigation measures are implemented;</li> <li>Prepare to increase the monitoring frequency to daily;</li> <li>Repeat measurement on next day of exceedance.</li> <li>Repeat <i>in situ</i> measurement</li> </ul>	• Discuss with ET and	<ul> <li>Discuss with IEC, ET and</li> </ul>	<ul> <li>Implement the agreed mitigation measures.</li> <li>Inform the SOR and</li> </ul>
sampling day	<ul> <li>to confirm findings;</li> <li>Identify reasons for non- compliance and source(s) of impact;</li> <li>Inform IEC Contractor and EPD;</li> <li>Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>Discuss mitigation measures with IEC, SOR and Contractor;</li> <li>Ensure mitigation measures are implemented;</li> <li>Increase the monitoring frequency to daily until no exceedance of Limit level.</li> </ul>	Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly; Assess the effectiveness of the implemented mitigation measures.	Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures.	<ul> <li>confirm notification of the non- compliance in writing;</li> <li>Rectify unacceptable practice;</li> <li>Check all plan and equipment;</li> <li>Consider changes of working methods;</li> <li>Discuss with ET, IEC and SOR and propose mitigation measures to IEC and SOR within three working days;</li> <li>Implement the agreed mitigation measures.</li> </ul>
Limit level being exceeded by more than one consecutive sampling day	<ul> <li>Repeat in situ measurement to confirm findings;</li> <li>Identify reasons for</li> </ul>	<ul> <li>Discuss with ET and</li> <li>Contractor on the mitigation measures;</li> <li>Review</li> </ul>	<ul> <li>Discuss with IEC, ET and Contractor on the proposed mitigation measures;</li> <li>Boguest</li> </ul>	Inform the SOR and confirm notification of the non- compliance in writing:
	non- compliance ent is owned by Fugro Technical S	proposals on mitigation	Request     Contractor to	writing; • Rectify

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. : +852-2450 8233 : +852-2450 6138 : matlab@fugro.com.hk : www.fugro.com



Event	ET Leader	IEC	SOR	Contractor
	<ul> <li>and source(s) of impact; Inform IEC Contractor and EPD;</li> <li>Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>Discuss mitigation measures with IEC, SOR and Contractor;</li> <li>Ensure mitigation measures are implemented;</li> <li>Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.</li> </ul>	measures submitted by Contractor and advise the SOR accordingly; Assess the effectiveness of the implemented mitigation measures.	<ul> <li>critically review the working methods;</li> <li>Make agreement on the mitigation measures to be implemented;</li> <li>Assess the effectiveness of the implemented mitigation measures;</li> <li>Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level.</li> </ul>	<ul> <li>unacceptable practice;</li> <li>Check all plant and equipment;</li> <li>Consider changes of working methods;</li> <li>Discuss with ET, IEC and SOR and propose mitigation measures to IEC and SOR within three working days;</li> <li>Implement the agreed mitigation measures;</li> <li>As directed by the SOR, to slow down or to stop all or part of the construction activities.</li> </ul>

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Appendix 6


**Figures** 

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone Telefax E-mail Website

: +852-2450 8233 : +852-2450 6138 : matlab@fugro.com.hk : www.fugro.com



Figure 1.1 WENT Landfill Consultation Zone

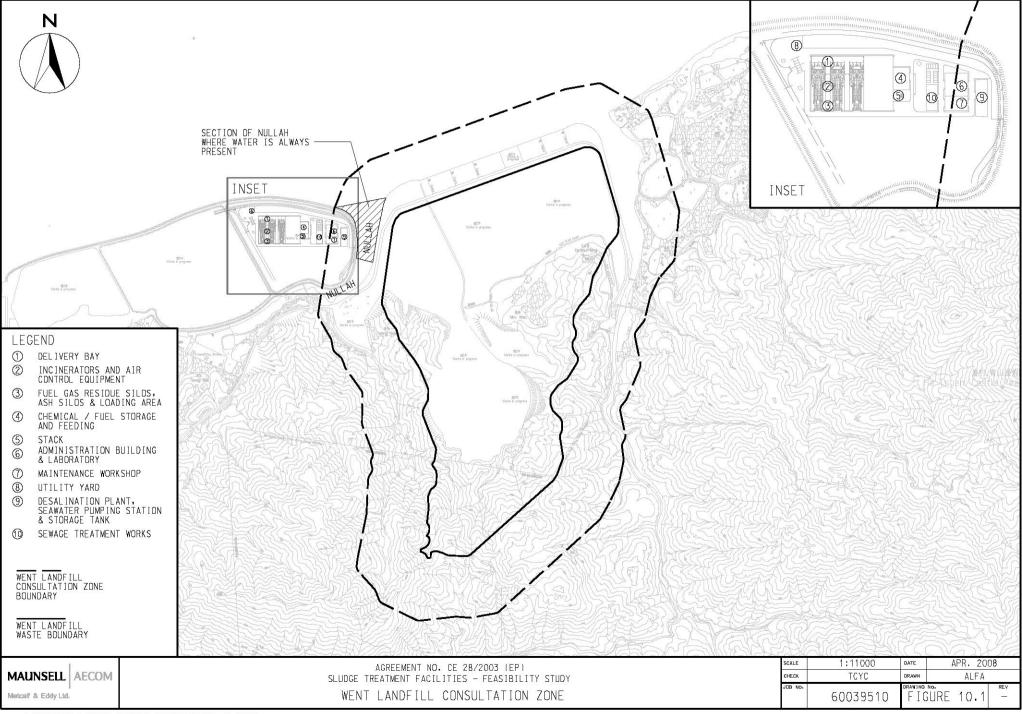


P:/60039510/1.01/CAD/DRAWING/REPORT/FIGURE 10.1.DGN

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone Telefax E-mail Website

: +852-2450 8233 : +852-2450 6138 : matlab@fugro.com.hk : www.fugro.com



Figure 3.1 Location of Project Site

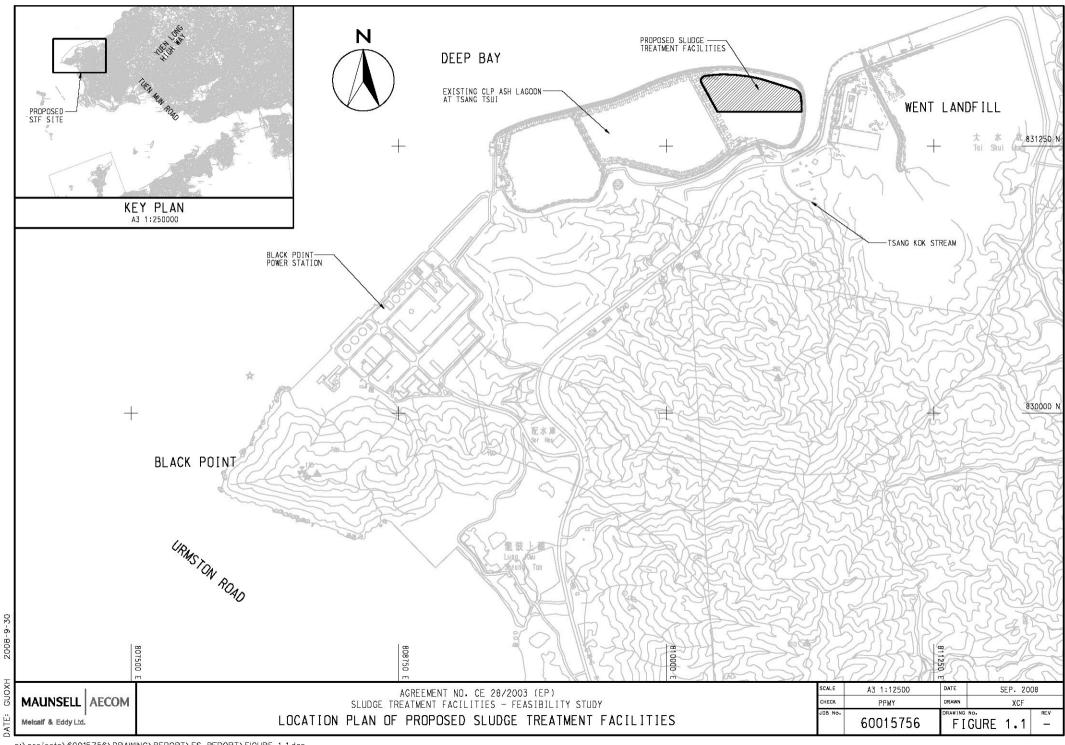

p:\projects\60015756\DRAWING\REPORT\ES\_REPORT\FIGURE\_1-1.dgn

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone Telefax E-mail Website

: +852-2450 8233 : +852-2450 6138 : matlab@fugro.com.hk : www.fugro.com



Figure 3.2 Project Organisation Structure

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. 
 Tel
 : +852-2450 8233


 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



#### **Management Structure and Organization Chart**

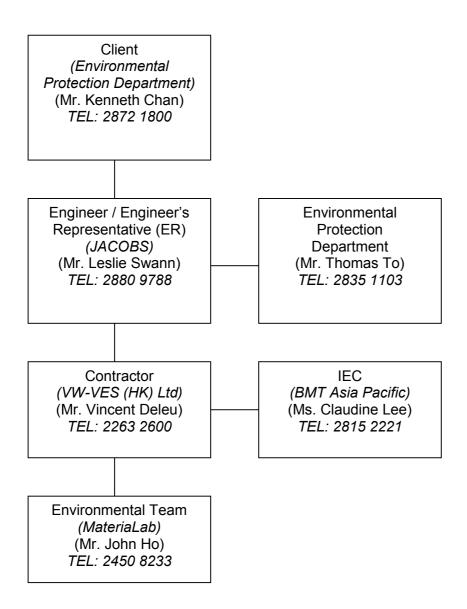

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. 

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk



Appendix 7

### **Work Program**

	nnted O n	: UZUEC1U		Ĩ		HON	G KON		DGE T ject O			IT FAG	CILITY	8	0	Date 2DEC10	V]H-₩-₽.	f-ZZ-000	Revision 1-D01			Checked RGU	Δ	Approved NP R
															-									_
		Activity Description	201 SEP OCT -1 1	10 NOV DEC 2 3	JAN FEB M	AR APR MA	2011 Y JUN JUL 9 10	AUG SEI	0CT NI	OV DEC	JAN FE	B MAR A	PR MAY	2012 JUN JUL A 21 22	UG SEP 23 24	0CT NOV 25 26	DEC JA	N FEB	AR APR 30 31	MAY JI 32 3	2013 UN JUL 33 34	AUG SEP 35 36	0CT 1 37	NOV DI 38 3
9       Non-series														0	-			0						
10 10											_													
Image: Second				_		_		. •			_	-		_					_		_			_
10 Notational and the second an		Print and the Depart of American Street Stre											- 🕹									_		-
Image: Appendix in the second of th																•								
Norway     Norway <td></td> <td></td> <td>-</td> <td>_</td> <td></td> <td>_</td> <td></td> <td></td> <td></td> <td>_</td> <td>_</td> <td></td> <td>_</td> <td></td> <td>_</td> <td></td> <td></td> <td></td> <td>_</td> <td></td> <td>_</td> <td></td> <td>-</td> <td>•</td>			-	_		_				_	_		_		_				_		_		-	•
Not where	ESIGN &	APPROVALS																						•
Note: Note:					() 							-	_	_	_				_		_	_		
10 10   10 <td></td>																								
10 Norwandow Norwandow   10 Norwandow	122-122 12		- 1																					
Image: Second				•																	_			
10     Review	160	Turbine		•																				
100     Norma     Norma <t< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></t<>																								
											-													
10       Non-2004         10	26.4	Foundations Plant A & B																						
300 Barbarbarbarbarbarbarbarbarbarbarbarbarba		Substructure + U G Utilities																						
200 Biological and a state of the sta	2040	Superstr (Roof) inc Glazing/Cladding - Area 1								ł														
20       Balance and a strain										-		TT												
30 Solvey Alexander	ACCE VALUE						1						1											
100 Source less starting 1										1														
20 Number landskame water in the second of the secon										ľ							-		_					++
100 <td>2020</td> <td>Process Train 1 Installation - Incin / Boiler</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>TT I</td> <td></td>	2020	Process Train 1 Installation - Incin / Boiler							TT I															
191 Northered with the set of the s								1																
100 Norway and the second of the secon																								
10 10	2038	1st Fire Sludge										1		T		•								
100 1000000000000000000000000000000000000	CONTRACTOR 00		-		_									1		1 1			-	Ť				
Not																								
30 Second 1 store 1 <		Superstr (Roof) - Area 4																						
Note:		Substructure + U G Utilities																						
Note:		Superstr (Roof) inc Glazing/Cladding - Area 1																						
100 1 <t< td=""><td></td><td></td><td></td><td></td><td></td><td>-</td><td></td><td></td><td></td><td></td><td>• • •</td><td></td><td></td><td></td><td>_</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>_</td><td></td></t<>						-					• • •				_								_	
20 Not how from from from from from from from from																								
900       9000000000000000000000000000000000000											1		111											
100 Norw York Varkalder, with York 1<	-		-	_									111										-	
9000       Pert To L Contractory Days       9000		10-34432-30542-400-400-400-400-								11														
900 Notation Landary Joug 900 90	120333		_						*		-													
1000 Now The Control 10000 1000 1000 1000 1000 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>_</td> <td></td> <td>-</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>T</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>							_		-						T									
101 <td></td> <td>-</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>-</td> <td></td> <td></td> <td></td>															-						-			
300 Battorylogic <t< td=""><td>S. 2011 12</td><td></td><td>-</td><td></td><td>_</td><td></td><td>-</td><td></td><td></td><td></td><td>_</td><td></td><td>- t</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>_</td><td></td></t<>	S. 2011 12		-		_		-				_		- t										_	
900 800 <td>YSTEM</td> <td>&amp; PLANT COMMISSIONING</td> <td>9</td> <td></td>	YSTEM	& PLANT COMMISSIONING	9																					
200 Requiring of a problem 1 <td< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></td<>																								
100 <td></td>																								
Ne LAY PURCHANNER NAKE EIG Separative fine de la construction de la c											-													
100 1000 </td <td></td> <td>1</td> <td></td> <td>_</td>													1											_
900 9000000000000000000000000000000000000																								
Nucleary UILDINGS - UILBAINE A 20       Nucleary UILBAINE A 20	6020	Superstructure									1													
<form>  1000000000000000000000000000000000000</form>	3-0-01+C - 17	and the second at the second																						
900 <td></td>																								
9000 Proces Exponentinization Plank B 0 <td< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>1 1</td><td>1</td><td></td><td></td><td></td><td></td><td></td><td></td><td>+</td><td></td><td></td><td></td><td></td><td></td><td></td></td<>										1 1	1							+						
mode mode<																								
1 1	7050	Process Equipment Installation Plant B																						
900 <td></td>																								
902 Signed function <																								
900 Process Equipment Installation   0010 Rode & Guipment Installation											1													
NULLARY BUILDING-CONDENSERA&B       Image: Condense A&B       Image: Condense AB       Image: Condense AB       Image: Conde																								
750       Just Just A & B       1	ICILLA	RY BUILDING - CONDENSER A & B																						
730       Installation Condense Plant A       1	10010010					_								_	_			++						
7330       Intallation Condense Plant B       1											-												-	
Stellwok Eredion Plant A       Acese Zabing & Plant B       Acese Zabing & Plant B <td< td=""><td>7530</td><td>Installation Condenser Plant B</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>1 1</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></td<>	7530	Installation Condenser Plant B											1 1											
8500       Access Cabling & Plyawork Plant A       Image: All and All										1														
B4F acade/Lide/gold/wy/Plart A       Image: Control of the contro of the control of the control of the control of the control of th	8520	Access Cabling & Pipework Plant A										2												
8700     Access Cabling & P joework Plant B     1 <t< td=""><td>8510</td><td>Ext Faca de/CladdingGallery Plant A</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td><math>+ \top</math></td><td></td><td><math>\square</math></td><td></td><td></td><td>_</td><td>_</td></t<>	8510	Ext Faca de/CladdingGallery Plant A																$+ \top$		$\square$			_	_
9800       Ext Faced & Flort Oatley Plant B       9													7											
9010     Foundations     Poundations	8560	Ext Facade & Fitout Gallery Plant B																						
9000     Subtructure																								
9020     Superstructure + Facade     9				-							_				_									-
XTERNAL WORKS	9020	Superstructure + Facade														L v								
10010 Roads & U/G Utilities													11					$\square$						
									+ +			+ +					-							
10030 Habitat 10020 SteLandscaping	10030	Habitat												1										
