### **Civil Engineering and Development Department**

EP-337/2009 & EP-445/2013/B


#### Contract No. KL/2014/01

Kai Tak Development – Stage 2 Infrastructure works for Developments at Southern Part of the Former Runway

Monthly EM&A Report

March 2023

(Version 1.0)



REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

CINOTECH CONSULTANTS LTD Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong Tel: (852) 2151 2083 Fax: (852) 3107 1388 Email: info@cinotech.com.hk







Our ref: 11-4-2023

11-4-2023

By email: clive.cheng@aecom-ktd.com and By hand

Supervising Officer Representative Aecom Asia Co Ltd. 8/F Grand Central Plaza Tower 2 138 Shatin Rural Committee Road Sha Tin, N.T. Hong Kong (Attn: Mr. Cheng Chi Hung)

Dear Mr. Cheng,

### Re: Contract No. KL/2014/01 (Environmental Permit Nos. EP-337/2009 and EP-445/2013/B) Kai Tak Development -- Stage 2 Infrastructure Works for Developments at Southern Part of the Former Runway Monthly EM&A report for March 2023 v1.0

Reference is made to the Environmental Team's submission of the Draft Monthly EM&A Report (Mar 2023 v1.0) provided to Independent Environmental Checker (IEC) via an email on 6-4-2023 for review and comment.

Please be informed that IEC has no adverse comment on the captioned submission. IEC hereby verifies the captioned submission in accordance with Specific Condition 2.2 of the Environmental Permit No. 337/2009 and 445/2013/B.

Thank you very much for your attention and please feel free to contact the undersigned should you require further information.

Yours faithfully,

For and on behalf of

Ka Shing Management Consultant Limited

lee Independent Environmental Checker

c.c.	CEDD	Mr. Jason Wong	(By email: kaichungwong@cedd.gov.hk)
	AECOM	Mr. Anthony Lok	(By email: anthony.lok@aecom-ktd.com)
	CEC-CCC	Mr. Eric Fong	(By email: eric-cs-fong@continental-engineering.com)
	Cinotech	Mr. K.S Lee	(By email: ks.lee@cinotech.com.hk)

Unit 2, 13/F Kai Yue Commercial Building, 2C Argyle St, Mong Kok, Kowloon 九龍旺角亞皆老街 2C 號啟如商業大廈 13 樓 2 室 Tel: (852) 2618 2166 Fax: (852) 2120 7752 Web Site: www.ka-shing.net 電話: (852) 2618 2166 傳真: (852) 2120 7752 網站: www.ka-shing.net



## TABLE OF CONTENTS

	EXECUTIVE SUMMARY	
	Introduction	
	Environmental Licenses and Permits	
	Key Information in the Reporting Month	
	Future Key Issues	
1.	INTRODUCTION4	ļ
	Background4	
	Project Organizations	
	Construction Activities undertaken during the Reporting Month	
	Summary of EM&A Requirements	
2.	AIR QUALITY	,
	Monitoring Requirements	
	Observations	
3.	NOISE	
	Monitoring Requirements	
	Observations	
4.	LANDSCAPE AND VISUAL9	1
	Monitoring Requirements	1
	Results and Observations	
5.	ENVIRONMENTAL AUDIT	
	Site Audits10	
	Status of Environmental Licensing and Permitting	
	Status of Waste Management	
	Implementation Status of Environmental Mitigation Measures	
	Summary of Mitigation Measures Implemented13	
	Implementation Status of Event Action Plans	
	Summary of Complaint, Warning, Notification of any Summons and Successful Prosecution	
6.	FUTURE KEY ISSUES14	
7.	CONCLUSIONS AND RECOMMENDATIONS16	
	Conclusions	ļ
	Recommendations16	I

### LIST OF TABLES

Table I	Non-compliance Recorded for the Project in the Reporting Month	2
	Summary Table for Key Information in the Reporting Month	
	Key Project Contacts	
	Construction Programme Showing the Inter-Relationship with Environmental Protection/Mitigation	
	Measures	6
Table V	Summary of Environmental Licensing and Permit Status	11
	Observations and Recommendations of Site Inspections	

#### LIST OF FIGURES

Figure 1 Site Layout Plan

#### LIST OF APPENDICES

А	Action an	d Limit	Levels
A	ACTION an		Levels

- B Summary of Exceedance
- C Site Audit Summary
- D Event Action Plans
- E Environmental Mitigation Implementation Schedule (EMIS)
- F Summaries of Environmental Complaint, Warning, Summon and Notification of Successful Prosecution
- G Waste Generated Quantity

#### **EXECUTIVE SUMMARY**

#### Introduction

- This is the 84<sup>th</sup> Monthly Environmental Monitoring and Audit Report prepared by Cinotech Consultants Ltd. for "Contract No. KL/2014/01 - Kai Tak Development – Stage 2 Infrastructure Works for Developments at the Southern Part of the Former Runway" (Hereafter referred to as "the Project"). This contract work comprises two Schedule 2 designated projects (DP), namely the new distributor road D4 (part) and roads D3A & D4A serving the planned KTD. The DPs are part of the designated projects under Environmental Permits (EP) No.: EP-337/2009 ("New distributor roads serving the planned Kai Tak Development") and EP-445/2013/B ("Kai Tak Development – Roads D3A & D4A") respectively. This report documents the findings of EM&A Works conducted in March 2023.
- 2. With reference to the same principle of EIA report of the Project, air quality monitoring station should be provided at the Air Sensitive Receivers (ASR) within 500 m from the boundary of this Project while construction noise monitoring station should be provided at the Noise Sensitive Receivers (NSR) within 300 m from the boundary of this Project. Since the opening of the Centre of Excellence in Paediatrics (Children's Hospital) on 18 December 2018, the hospital is considered as the only relevant monitoring location and therefore the monitoring is required.
- 3. The major site activities undertaken in the reporting month included:
  - Architectural features works at ground floor open space;
  - DCS modification works at Shing Fung Road;
  - Defect rectification works of pedestrian streets;
  - Minor E&M works;
  - Deck movement joint rectification
  - TTA implementation for minor works at Shing Fung Road and;
  - Deck cladding rectification and modification.

#### **Environmental Monitoring Works**

- 4. Environmental monitoring for the Project was performed in accordance with the EM&A Manual and the monitoring results were checked and reviewed. Site Inspections/Audits were conducted once per week. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.
- 5. Summary of the non-compliance in the reporting month for the Project is tabulated in **Table I**.

Parameter	No. of Project-rela	No. of Project-related Exceedance	
rarameter	Action Level	Limit Level	Action Taken
Noise	0	0	N/A

Table I         Non-compliance Recorded for the Project in the Reporting Month
--

Environmental Monitoring for Air Quality and Construction Noise

6. No monitoring for air quality and construction noise is required. No Action/Limit Level exceedance was recorded.

#### **Environmental Licenses and Permits**

- Licenses/Permits granted to the Project include the Environmental Permits (EP) for the Project, EP-337/2009 issued on 23 April 2009 and EP-445/2013 issued on 3 May 2013 (Amended Environmental Permit (No.: EP-445/2013/A) issued on 13 August 2014; further amendment of Environmental Permit (No.: EP-445/2013/B) issued on 3 May 2022).
- 8. Billing Account for Disposal of Construction Waste (A/C No. 7024073).
- 9. Registration of Chemical Waste Producer (License: 5213-247-C4004-01).
- 10. Water Discharge License (License: WT0029931-2017).
- 11. Construction Noise Permits (Permit: GW-RE0442-20, GW-RE0639-20, GW-RE0045-21, GW-RE0717-21 & GW-RE0656-21).

#### Key Information in the Reporting Month

12. Summary of key information in the reporting month is tabulated in Table II.

Event	Event	Details	Action Taken	Status	Remark
	Number	Nature			
Complaint received	0		N/A	N/A	
Reporting Changes	0		N/A	N/A	
Notifications of any summons & prosecutions received	0		N/A	N/A	

 Table II
 Summary Table for Key Information in the Reporting Month

#### Future Key Issues

13. The future key environmental issues in the coming month include:

- Wastewater and runoff discharge from site;
- Noise from operation of the equipment, especially for rock-breaking activities, and machinery on-site;
- Dust generation from stockpiles of dusty materials, exposed site area, excavation works and rock breaking activities;
- Dust generating activity and on haul road;
- Storage of construction materials on site;
- Storage of chemicals/fuel and chemical waste/waste oil on site;
- Accumulation of general and construction waste on site.

#### **Reporting Changes**

14. Since the major parts of Works under Contract no. KL/2014/03 has been completed, the environmental monitoring works of EM&A monitoring station, KTD1a, was then handed over to the ET of Contract no. ED/2018/04 in August, 2020. In order to obtain the environmental impact monitoring data with higher representativeness based on several factors, such as distance between monitoring location and the sensitive receiver, non-project related interference, obstruction to the construction works on site and the power supply problem, the monitoring location KTD1a was relocated to the original location as proposed in the EM&A manual (AEIAR-174/2013), and renamed as KTD1 on 3 August 2020.

#### 1. INTRODUCTION

#### Background

- 1.1 The Kai Tak Development (KTD) is located in the south-eastern part of Kowloon Peninsula, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling. It covers a land area of about 328 hectares. Stage 2 Infrastructure Works for Developments for Southern Part of the Former Runway is one of the construction stages of KTD. It contains two Schedule 2 DPs including new distributor roads serving the planned KTD and KTD Roads D3A & D4A. The general layout of the Project is shown in **Figure 1.**
- 1.2 One Environmental Permit (EP) No.: EP-337/2009 was issued on 23 April 2009 for new distributor roads serving the planned KTD and one Environmental Permit No.: EP-445/2013 was issued on 3 May 2013 for Kai Tak Development Roads D3A & D4A to Civil Engineering and Development Department (CEDD) as the Permit Holder. Pursuant to Section 13 of the EIAO, the Director of Environmental Protection Department amended the Environmental Permit No.: EP-445/2013 based on the Application No. VEP-449/2014 and the Environmental Permit (No.: EP-445/2013/A) was issued on 13 August 2014. The Environmental Permit (No.: EP-445/2013/A) was further amended and the Environmental Permit (No.: EP-445/2013/B) was issued on 3 May 2022.
- 1.3 A study of environmental impact assessment (EIA) was undertaken to consider the key issues of air quality, noise, water quality, waste, land contamination, cultural heritage and landscape and visual impact, and identify possible mitigation measures associated with the works. EIA Reports (Register No. AEIAR-130/2009 and AEIAR-170/2013) were approved by the Environmental Protection Department (EPD) on 4 March 2009 and 3 May 2013 respectively.
- 1.4 Cinotech Consultants Limited (Cinotech) was commissioned by Civil Engineering and Development Department (CEDD) to undertake the role of the Environmental Team (ET) for the Contract No. KL/2014/01 Stage 2 Infrastructure Works for Developments at the Southern Part of the Former Runway. The construction work under KL/2014/01 comprises the construction of part of the Road D4 under the EP (EP-337/2009) and the construction of Roads D3A & D4A under the EP (EP-445/2013/B).
- 1.5 Cinotech Consultants Limited was commissioned by Civil Engineering and Development Department (CEDD) to undertake the Environmental Monitoring and Audit (EM&A) works for the Project. The construction commencement of this Contract is on 13 April 2016. This is the 84<sup>th</sup> Monthly EM&A report summarizing the EM&A works for the Project in March 2023.
- 1.6 All project information since the commencement of work under EPs including Monthly EM&A Reports is made available to the public via internet access at the website: https://www.epd.gov.hk/eia/english/register/index8/vep4492014\_content.html

#### **Project Organizations**

- 1.7 Different parties with different levels of involvement in the project organization include:
  - Project Proponent Civil Engineering and Development Department (CEDD).
  - The Supervising Officer and the Supervising Officer's Representative (SO) AECOM Asia Co. Ltd. (AECOM).
  - Environmental Team (ET) Cinotech Consultants Limited (CCL).
  - Independent Environmental Checker (IEC) Ka Shing Management Consultant Ltd. (KSMC).
  - Contractor Continental Engineering Corp. and Chit Cheung Construction Co. Ltd. Joint Venture (CCJV).
- 1.8 The key contacts of the Project are shown in **Table III.**

**Table III** 

**Key Project Contacts** 

Party	Role	Contact Person	Position	Phone No.	Fax No.
CEDD	Project Proponent	Mr. Michael So	Engineer	3579 2066	27390076
AECOM	Supervising Officer	Mr. Anthony Lok	SRE	3746 1801	2798 0783
Cinotech	Environmental Team	Mr. K S Lee	Environmental Team Leader	2151 2091	
		Ms. Betty Choi	Audit Team Leader	2151 2072	3107 1388
KSMC	Independent Environmental Checker	Mr. Happy Lee	IEC	2618 2166	2120 7752
CCJV	Contractor	Mr. Simon Yau	Environmental Officer	2960 1398	2960 1399

#### Construction Activities undertaken during the Reporting Month

- 1.9 The site activities undertaken in the reporting month included:
  - Architectural features works at ground floor open space;
  - DCS modification works at Shing Fung Road;
  - Defect rectification works of pedestrian streets;
  - Minor E&M works;
  - Deck movement joint rectification
  - TTA implementation for minor works at Shing Fung Road and;
  - Deck cladding rectification and modification.

1.10 The construction programme showing the inter-relationship with environmental protection/mitigation measures is presented in **Table IV**.

Table IV	<b>Construction Programme Showing the Inter-Relationship with Environmental</b>				
Protection/Mitigation Measures					

Construction Works	Major Environmental Impact	Control Measures
As mentioned in Section 1.8	Noise, dust impact, water quality and waste generation	<ul> <li>Sufficient watering of the works site with active dust emitting activities;</li> <li>Properly cover the stockpiles;</li> <li>On-site waste sorting and implementation of trip ticket system;</li> <li>Appropriate desilting/sedimentation devices provided on site for treatment before discharge;</li> <li>Use of quiet plant and well-maintained construction plant;</li> <li>Provide mitigation measure to temporary use of chemicals;</li> <li>Provide sufficient mitigation measures as recommended in Approved EIA Report/Lease requirement.</li> </ul>

#### Summary of EM&A Requirements

- 1.11 The EM&A programme requires construction noise monitoring, air quality monitoring, landscape and visual monitoring and environmental site audit. The EM&A requirements for each parameter are described in the following sections, including:
  - All monitoring parameters;
  - Action and Limit levels for all environmental parameters;
  - Event Action Plans;
  - Environmental requirements and mitigation measures, as recommended in the EM&A Manual under the EP.
- 1.12 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 5 of this report.

### 2. AIR QUALITY

#### **Monitoring Requirements**

- 2.1 With reference to the same principle of EIA report of the Project, air quality monitoring station should be provided at the Air Sensitive Receivers (ASR) within 500 m from the boundary of this Project. Since the opening of the Centre of Excellence in Paediatrics (Children's Hospital) on 18 December 2018, the hospital is considered as the only relevant monitoring location and therefore the monitoring is required.
- 2.2 As the monitoring works for the hospital is covered by the Contract KL/2014/03 (Kai Tak Development Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway) at the monitoring station (KTD1), the corresponding monitoring results for January 2023 should be accessed in the EM&A report for the reporting month. Appendix A shows the established Action and Limit Levels for the environmental monitoring works.

#### Observations

- 2.3 No monitoring for air quality is required for this report. No Action/Limit Level exceedance at KTD1 was recorded. The summary of exceedance record in reporting month is shown in **Appendix B**.
- 2.4 Site audits were carried out on a weekly basis to monitor and audit the timely implementation of air quality mitigation measures within the site boundaries of this Project. The summaries of site audits are attached in **Appendix C.**

#### 3. NOISE

#### **Monitoring Requirements**

- 3.1 With reference to the same principle of EIA report of the Project, construction noise monitoring station should be provided at the Noise Sensitive Receivers (NSR) within 300 m from the boundary of this Project. Since the opening of the Centre of Excellence in Paediatrics (Children's Hospital) on 18 December 2018, the hospital is considered as the only relevant monitoring location and therefore the monitoring is required.
- 3.2 As the monitoring works for the hospital is covered by the Contract KL/2014/03 (Kai Tak Development Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway) at the monitoring station (KTD1), the corresponding monitoring results for March 2023 should be accessed in the EM&A report for the reporting month. **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.

#### Observations

- 3.3 No monitoring for construction noise is required for this report. No Action/Limit Level exceedance at KTD1 was recorded. The summary of exceedance record in reporting month is shown in **Appendix B**.
- 3.4 Site audits were carried out on a weekly basis to monitor and audit the timely implementation of construction noise mitigation measures within the site boundaries of this Project. The summaries of site audits are attached in **Appendix C**.

#### 4. LANDSCAPE AND VISUAL

#### **Monitoring Requirements**

4.1 According to EM&A Manual of the Kai Tak Development EIA Study, ET shall monitor and audit the contractor's operation during the construction period on a weekly basis, and to report on the contractor's compliance.

#### **Results and Observations**

- 4.2 Site audits were carried out on a weekly basis to monitor and audit the timely implementation of landscape and visual mitigation measures within the site boundaries of this Project. The summaries of site audits are attached in **Appendix C**.
- 4.3 No non-compliance of the landscape and visual impact was recorded in the reporting month.
- 4.4 Should non-compliance of the landscape and visual impact occur, action in accordance with the action plan presented in **Appendix D** shall be performed.

#### 5. ENVIRONMENTAL AUDIT

#### Site Audits

- 5.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix C**.
- 5.2 Site audits were conducted by representatives of the Contractor, Supervising Officer and ET on 2, 7, 16, 22 & 29 March 2023 in the reporting month. IEC joint site inspection was conducted on 29 March 2023. No non-compliance was observed during the site audits.

#### Status of Environmental Licensing and Permitting

5.3 All permits/licenses obtained for the Project are summarized in **Table V**.

Table V	Summary of Environmental Licensing and Permit Status				
Permit No.	Valid	Period	Details	Status	
I CI IIII INO.	From	То	Details	Status	
<b>Environmental Pe</b>	ermit (EP)				
EP-337/2009	23 Apr 2009	N/A	Construction of new distributor roads serving the planned Kai Tak development.	Valid	
EP-445/2013/A	13 Aug 2014	N/A	Construction of Kai Tak Development roads D3A and D4A	Valid	
EP-445/2013/B	3 May 2022	N/A	Construction of Kai Tak Development roads D3A and D4A	Valid	
Effluent Discharge	License		1		
WT00023634- 2016		31 Mar 2021	Wastewater from the construction site including effluent treated by screen and sedimentation tank; There are no more need for the license after 31 March 2021 as the project is close to completion and no significant waste water is being generated from site.	Expired on 31 Mar 2021	
WT0029931-2017		31 December 2022	Wastewater from the construction site including effluent treated by screen and sedimentation tank; There are no more need for the license after 31 December 2022 as the project is close to completion and no significant waste water is being generated from site.	Expired on 31 December 2022	
<b>Registration of Che</b>	emical Waste	Producer			
5213-247-C4004- 01		N/A	Chemical Waste Types: Surplus paint, waste contaminated by paint, diesel, waste contaminated by diesel, spent lubricating oil and waste, soil contaminated by lubricating oil.	Valid	
Construction Noise Permit (CNP)					
GW-RE0442-20	14 Jun 2020	13 Dec 2020	Construction Noise Permit for the use of powered mechanical equipment for carrying out construction work other than percussive pilling and performing	Expired on 13 Dec 2020	
GW-RE0639-20	3 Aug 2020	19 Jan 2021	prescribed construction work. Construction Noise Permit for the use of powered mechanical	Expired on 19 Feb 2021	

#### Table V Summary of Environmental Licensing and Permit Status

Permit No.	Valid	Period	Details	Status
rernit No.	From	То	Details	Status
GW-RE0045-21	20 Jan 2021	19 Jul 2021	equipment for carrying out construction work other than percussive pilling and performing prescribed construction work.	Expired on 19 Jul 2021
GW-RE0656-21	9 Jul 2021	30 Sep 2021		Expired on 30 Sep 2021
GW-RE0717-21	30 Jul 2021	19 Jan 2022		Expired on 19 Jan 2022

#### **Status of Waste Management**

- 5.4 The amount of wastes generated by the major site activities of this Project during the reporting month is shown in **Appendix G**.
- 5.5 In respect of the dump truck cover, the Contractor is reminded to take record photos and inspection to ensure that all dump trucks have fully covered the skip before leaving the site.

#### **Implementation Status of Environmental Mitigation Measures**

5.6 During site inspections in the reporting month, no non-conformance was identified. ET weekly site inspections were carried out during the reporting month and the observations and recommendations are summarized in **Table VI**.

Parameters	Date	Observations and Recommendations	Follow-up
Water Quality			
Air Quality			
Noise			
Waste/ Chemical Management			
Landscape and Visual			
Permits/ Licenses			

Table VI	<b>Observations and Recommendations of Site Inspections</b>
----------	---

#### **Summary of Mitigation Measures Implemented**

5.7 An updated summary of the EMIS is provided in **Appendix E**.

#### **Implementation Status of Event Action Plans**

5.8 The Event Action Plans for noise and landscape and visual are presented in AppendixD. No Event Action Plan for air quality is considered necessary.

#### Construction Dust

5.9 No Action/Limit Level exceedance was recorded in the reporting month.

#### Construction Noise

5.10 No Action/Limit Level exceedance was recorded in the reporting month.

#### Landscape and visual

5.11 No non-compliance was recorded in the reporting month.

# Summary of Complaint, Warning, Notification of any Summons and Successful Prosecution

5.12 The summaries of environmental complaint, warning, summon and notification of successful prosecution for the Project is presented in **Appendix F**.

13

#### 6. FUTURE KEY ISSUES

- 6.1 Major site activities undertaken for the coming two months include:
  - Architectural features works at ground floor open space;
  - Defect rectification works of pedestrian streets & at deck level;
  - Minor E&M works;
  - Installation of DCS louvres & Laying of paving blocks for footpath;
  - Deck cladding rectification and modification;
  - Deck movement joint rectification;
  - Planting works at roundabout & footpath;
  - TTA implementation for minor works at Shing Fung Road, and;
  - TTA implementation, minor works at Wang Chiu Road / Kai Cheung Road
- 6.2 Key environmental issues in the coming month include:
  - Wastewater and runoff discharge from site;
  - Silt, mud and sand along u-channels and sedimentation tanks;
  - Noise from operation of the equipment, especially for rock-breaking activities and machinery on-site;
  - Dust generation from stockpiles of dusty materials, exposed site area, excavation works and rock breaking activities;
  - Storage of construction materials on site;
  - Storage of chemicals/fuel and chemical waste/waste oil on site;
  - Accumulation of general and construction waste on site

6.3 The tentative program of major site activities and the impact prediction and control measures for the coming two months, i.e. April & May 2023 are summarized as follows:

Construction Works	Major Impact Prediction	Control Measures
	Air quality impact (dust)	<ul><li>a) Frequent watering or covering stockpiles with tarpaulin or similar means; and</li><li>b) Watering of any earth moving activities.</li></ul>
	Water quality impact (surface run-off)	<ul> <li>a) Provision of perimeter protection such as sealing of hoarding footings to avoid run-off from entering the existing storm water drainage system via public road; and</li> <li>b) Provision of measures to prevent discharge into the stream.</li> </ul>
As mentioned in Section 6.1	Noise Impact	<ul> <li>a) Scheduling of noisy construction activities if necessary to avoid persistent noisy operation;</li> <li>b) Controlling the number of plants use on site;</li> <li>c) Regular maintenance of machines; and</li> <li>d) Use of acoustic barriers if necessary.</li> </ul>
	Waste/ Chemical Management	<ul> <li>a) Maintenance involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.</li> <li>b) Chemical wastes should be hold by suitable containers with clear label and stored at a safe location.</li> </ul>

#### 7. CONCLUSIONS AND RECOMMENDATIONS

#### Conclusions

7.1 The Environmental Monitoring and Audit (EM&A) Report presents the EM&A works undertaken in March 2023.

#### Air Quality and Construction Noise

7.2 No regular monitoring air quality and noise monitoring is required for the Project. No Action/Limit Level exceedance was recorded.

Landscape and visual

7.3 No non-compliance was recorded in the reporting month.

#### Complaint and Prosecution

- 7.4 No environmental complaints and environmental prosecution were received in the reporting month.
- 7.5 The ET will keep track on the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

#### Recommendations

7.6 According to the environmental audit performed in the reporting month, the following recommendations were made:


Waste/ chemical management

- To avoid the accumulation of general refuse, especially cigarette butt and other domestic waste.
- The construction/chemical material should be stoned at the proper place.
- The drip trays with adequate capacity and well maintained should be provided to chemicals

#### Air Quality

• The dusty material should be covered by impervious materials or maintained wet.

FIGURES

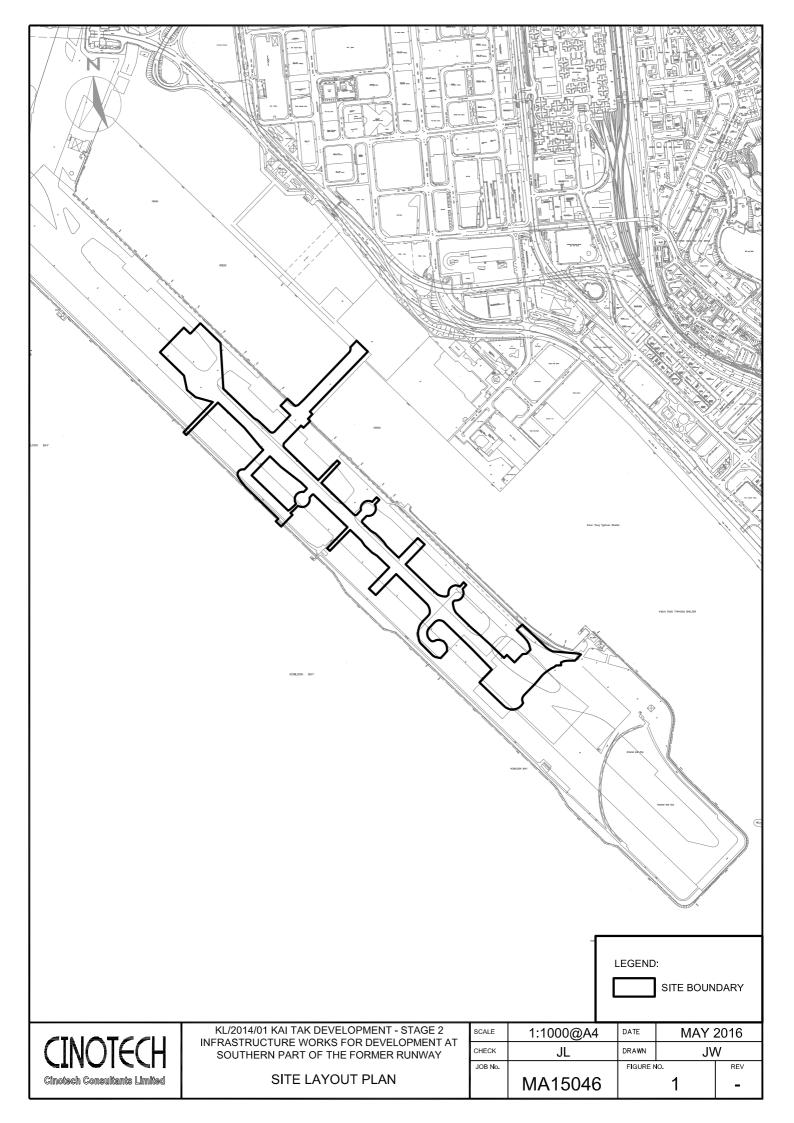

APPENDIX A ACTION AND LIMIT LEVELS

### **Appendix A - Action and Limit Levels**

Monitoring Station	Parameter	Action Level (µg/ m <sup>3</sup> )	$      Limit \ Level^{(1)(2)} \\ (\mu g/\ m^3) $
KTD1	24-hr TSP	177	260
KTD1*	1-hr TSP	285	500

#### Table A-1 Action and Limit Levels for Air Quality Monitoring

\* 1-hr TSP monitoring should be required in case of complaints.

Table A-2	Action and Limit Levels for Construction Noise Monitoring	
I abit A-2	Action and Limit Levels for Construction Noise Monitoring	

Time Period	Action Level	Limit Level <sup>(1)(2)</sup>
0700-1900 hrs on normal weekdays	When one documented complaint is received	75 dB(A) 70dB(A)/65dB(A)*

Remarks: (1) If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

(2) No regular noise impact monitoring station for this Contract. It is subject to the noise sensitive receiver(s) and additional monitoring work.

(\*) 70dB(A) and 65dB(A) for schools during normal teaching periods and school examination periods respectively.

APPENDIX B SUMMARY OF EXCEEDANCE

### Contract No. KL/2014/01 Kai Tak Development –Stage 2 Infrastructure Works for Developments at the Southern Part of the Former Runway

**Appendix B – Summary of Exceedance** 

Exceedance Record for Contract No. KL/2014/01

Reporting Month: March 2023

#### (A) Exceedance Record for Construction Dust

(NIL in the reporting month)

#### (B) Exceedance Record for Construction Noise

(NIL in the reporting month)

(C) Exceedance Record for Landscape and Visual

(NIL in the reporting month)

APPENDIX C SITE AUDIT SUMMARY

Checklist Reference Number	230302
Date	02 March 2023 (Thursday)
Time	13:30 - 14:30

		Related
Ref. No.	Non-Compliance	Item No
-	None identified	-
		Related
Ref. No.	Remarks/Observations	Item No
	B. Water Quality	
	No environmental deficiency was identified during site inspection	
	C. Air Quality	
	No environmental deficiency was identified during site inspection.	
	D. Noise	
	No environmental deficiency was identified during site inspection.	
	E. Waste / Chemical Management	
	No environmental deficiency was identified during site inspection.	
	F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits /Licenses	
	No environmental deficiency was identified during site inspection.	
	H. Others	
	No follow-up items are required from the previous site inspection (ref no.: 230222).	

	Name	Signature	Date
Recorded by	Charles Fung	Quan	02 March 2023
Checked by	Colman Wong	Colman	06 March 2023

Checklist Reference Number	230307
Date	07 March 2023 (Tuesday)
Time	13:30 - 14:30

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
		Related
Ref. No.	Remarks/Observations	Item No.
	B. Water Quality	
	No environmental deficiency was identified during site inspection	
	C. Air Quality	
	No environmental deficiency was identified during site inspection.	
	D. Noise	
	No environmental deficiency was identified during site inspection.	
	E. Waste / Chemical Management	
	No environmental deficiency was identified during site inspection.	
	F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits /Licenses	
	No environmental deficiency was identified during site inspection.	
	H. Others	
	No follow-up items are required from the previous site inspection (ref no.: 230302).	

	Name	Signature	Date
Recorded by	KK Kwan	MJL Thesan	07 March 2023
Checked by	Colman Wong	Colman	13 March 2023

Checklist Reference Number	230316
Date	16 March 2023 (Tuesday)
Time	13:30 - 14:30

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	B. Water Quality	
	No environmental deficiency was identified during site inspection	
	C. Air Quality	
	No environmental deficiency was identified during site inspection.	
	D. Noise	
	No environmental deficiency was identified during site inspection.	
	E. Waste / Chemical Management	
	No environmental deficiency was identified during site inspection.	
	F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits /Licenses	
	No environmental deficiency was identified during site inspection.	
	H. Others	
	No follow-up items are required from the previous site inspection (ref no.: 230307).	

	Name	Signature	Date
Recorded by	KK Kwan	MJL Thesan	16 March 2023
Checked by	Colman Wong	Colman	20 March 2023

Checklist Reference Number	230322
Date	22 March 2023 (Tuesday)
Time	13:30 - 14:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
	None dentified	Related
Ref. No.	Remarks/Observations	Item No.
	B. Water Quality	
	No environmental deficiency was identified during site inspection	
	C. Air Quality	
	No environmental deficiency was identified during site inspection.	
	D. Noise	
	No environmental deficiency was identified during site inspection.	
	E. Waste / Chemical Management	
	No environmental deficiency was identified during site inspection.	
	• F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits /Licenses	
	No environmental deficiency was identified during site inspection.	
	H. Others	
	No follow-up items are required from the previous site inspection (ref no.: 230316).	

	Name	Signature	Date
Recorded by	KK Kwan	Mr. Human	22 March 2023
Checked by	Colman Wong	Colman	27 March 2023

Checklist Reference Number	230329
Date	29 March 2023 (Wednesday)
Time	14:30 - 15:30

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
	None dentified	Related
Ref. No.	Remarks/Observations	Item No.
	B. Water Quality	
	No environmental deficiency was identified during site inspection	
	C. Air Quality	
	No environmental deficiency was identified during site inspection.	
	D. Noise	
	No environmental deficiency was identified during site inspection.	
	E. Waste / Chemical Management	
	No environmental deficiency was identified during site inspection.	
	• F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits /Licenses	
	No environmental deficiency was identified during site inspection.	
	H. Others	
	No follow-up items are required from the previous site inspection (ref no.: 230322).	

	Name	Signature	Date
Recorded by	Charles Fung	Quan	29 March 2023
Checked by	Colman Wong	Colman	03 April 2023

APPENDIX D EVENT ACTION PLANS

## **Appendix D - Event Action Plans**

Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	<ol> <li>Notify ER, IEC and Contractor;</li> <li>Carry out investigation;</li> <li>Report the results of investigation to the IEC, ER and Contractor;</li> <li>Discuss with the IEC and Contractor on remedial measures required;</li> <li>Increase monitoring frequency to check mitigation effectiveness.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Review the investigation results submitted by the ET;</li> <li>Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Supervise the implementation of remedial measures.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Submit noise mitigation proposals to IEC and ER;</li> <li>Implement noise mitigation proposals.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>
Limit Level being exceeded	<ol> <li>Inform IEC, ER, Contractor and EPD;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency;</li> <li>Identify source and investigate the cause of exceedance;</li> <li>Carry out analysis of Contractor's working procedures;</li> <li>Discuss with the IEC, Contractor and ER on remedial measures required;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>If exceedance stops, cease additional monitoring.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Supervise the implementation of remedial measures;</li> <li>If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC and ER within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Submit further proposal if problem still not under control;</li> <li>Stop the relevant portion of works as instructed by the ER until the exceedance is abated.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>

## **Appendix D - Event Action Plans**

## Event/Action Plan for Landscape and Visual

EVENT ACTION	ACTION				
LEVEL	ET	IEC	ER	CONTRACTOR	
Design Check	<ul> <li>Check final design conforms to the requirements of EP and prepare report.</li> </ul>	<ul> <li>Check report.</li> <li>Recommend remedial design if necessary</li> </ul>	<ul> <li>Undertake remedial design if necessary</li> </ul>		
Non- conformity on one occasion	<ul> <li>Identify Source</li> <li>Inform IEC and ER</li> <li>Discuss remedial actions with IEC, ER and Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> </ul>	<ul> <li>Check report</li> <li>Check Contractor's working method</li> <li>Discuss with ET and Contractor on possible remedial measures</li> <li>Advise ER on effectiveness of proposed remedial measures.</li> <li>Check implementatio n of remedial measures.</li> </ul>	<ul> <li>Notify Contractor</li> <li>Ensure remedial measures are properly implemented</li> </ul>	<ul> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ul>	
Repeated Non- conformity	<ul> <li>Identify Source</li> <li>Inform IEC and ER</li> <li>Increase monitoring frequency</li> <li>Discuss remedial actions with IEC, ER and Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> <li>If non- conformity stops, cease additional monitoring</li> </ul>	<ul> <li>Check monitoring report</li> <li>Check Contractor's working method</li> <li>Discuss with ET and Contractor on possible remedial measures</li> <li>Advise ER on effectiveness of proposed remedial measures</li> <li>Supervise implementatio n of remedial measures.</li> </ul>	<ul> <li>Notify Contractor</li> <li>Ensure remedial measures are properly implemented</li> </ul>	<ul> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ul>	

APPENDIX E ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE (EMIS)

EIA Ref.	Mitigation Measures	Status
Construction Air Qu	ality	·
S3.2 (AEIAR-130/2009)	8 times daily watering of the work site with active dust emitting activities.	٨
S4.8 (AEIAR-170/2013)	Control measures stipulated in the approved KTD Schedule 3 EIA Report should be strictly followed.	٨
S3.2 (AEIAR-130/2009) and S4.8	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimize cumulative dust impacts.	
(AEIAR-170/2013)	<ul> <li>Stockpiling site(s) should be lined with impermeable sheeting and bunded. Stockpiles should be fully covered by impermeable sheeting to reduce dust emission.</li> <li>Misting for the dusty material should be carried out before being loaded into the vehicle.</li> </ul>	∧ ∧
	<ul> <li>Any vehicle with an open load carrying area should have properly fitted side and tail boards.</li> </ul>	٨
	• Material having the potential to create dust should not be loaded from a level higher than the side and tail boards and should be dampened and covered by a clean tarpaulin.	٨
	• The tarpaulin should be properly secured and should extent at least 300 mm over the edges of the sides and tailboards. The material should also be dampened if necessary before transportation.	٨
	• The vehicles should be restricted to maximum speed of 10 km per hour and confined haulage and delivery vehicle to designated roadways insider the site. Onsite unpaved roads should be compacted and kept free of lose materials.	<b>^</b>
	• Vehicle washing facilities should be provided at every vehicle exit point.	٨

## Appendix E - Summary of Implementation Schedule of Mitigation Measures for Construction Phase

EIA Ref.	Mitigation Measures	Status
	<ul> <li>The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.</li> <li>Every main haul road should be scaled with concrete and kept clear of dusty materials or sprayed with water so as to maintain the entire road surface wet.</li> <li>Every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the three sides; and</li> <li>Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites.</li> </ul>	
Construction Noise		
S3.3 (AEIAR-130/2009)	Use of quiet PME, movable barriers barrier for Asphalt Paver, Breaker, Excavator and Hand-held breaker and full enclosure for Air Compressor, Bar Bender, Concrete Pump, Generator and Water Pump.	<u>л</u>
S3.3 (AEIAR-130/2009)	Good Site Practice:	
(ALIAK-130/2007)	• Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program.	٨
	• Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program.	٨
	<ul> <li>Mobile plant, if any, should be sited as far away from NSRs as possible.</li> </ul>	٨
	<ul> <li>Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum.</li> </ul>	٨
	• Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	٨
	• Material stockpiles and other structures should be effectively utilized, wherever	^

EIA Ref.	Mitigation Measures	Status
	practicable, in screening noise from on-site construction activities.	
S3.3 (AEIAR-130/2009)	Scheduling of Construction Works during School Examination Period	N/A
S3.8 (AEIAR-170/2013)	Provision of a landscaped deck along Roads D3A & D4A.	N/A
S3.8 (AEIAR-170/2013)	<ul> <li>Provision of about 1090 m length of vertical noise barrier (connected to the deck) at Roads D3A &amp; D4A;</li> <li>Provision of about 60 m length of overhang vertical noise barrier (connected to the deck) at Road D4A; and</li> <li>Provision of staircases with noise barriers next to Sites 4A1 and 4B1</li> <li>It should be noted that the exact length of the mitigation measures would be subject to minor refinement during the detailed design stage.</li> </ul>	N/A N/A N/A
S3.8 (AEIAR-170/2013)	Non-noise sensitive use areas within Sites 4A1 and 4B1.	N/A
S3.8 (AEIAR-170/2013)	Avoid sensitive façade with openable window facing Road D3A.	N/A
<b>Construction Water</b>	Quality	
S3.4 (AEIAR-130/2009) and S5.8 (AEIAR-170/2013)	<ul> <li><u>Construction Runoff</u></li> <li>Exposed soil areas should be minimised to reduce the potential for increased siltation, contamination of runoff, and erosion. Construction runoff related impacts associated with the above ground construction activities can be readily controlled through the use of appropriate mitigation measures which include:         <ul> <li>use of sediment traps</li> <li>adequate maintenance of drainage systems to prevent flooding and overflow</li> </ul> </li> </ul>	∧ ∧

EIA Ref.	Mitigation Measures	Status
	Construction site should be provided with adequately designed perimeter channel and pre- treatment facilities and proper maintenance. The boundaries of critical areas of earthworks should be marked and surrounded by dykes or embankments for flood protection. Temporary ditches should be provided to facilitate runoff discharge into the appropriate watercourses, via a silt retention pond. Permanent drainage channels should incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94.	٨
	Ideally, construction works should be programmed to minimise surface excavation works during the rainy season (April to September). All exposed earth areas should be completed as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means.	٨
S5.8 (AEIAR-170/2013)	Earthworks final surfaces should be well compacted and the subsequent permanent work or surface protection should be carried out immediately after the final surfaces are formed to prevent erosion caused by rainstorms. Appropriate drainage like intercepting channels should be provided where necessary.	٨
	Measures should be taken to minimize the ingress of rainwater into trenches. If excavation of trenches in wet seasons is necessary, they should be dug and backfilled in short sections. Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.	٨
S3.4 (AEIAR-130/2009)	Sediment tanks of sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m <sup>3</sup> capacity, are recommended as a general mitigation measure	٨

EIA Ref.	Mitigation Measures	Status
	which can be used for settling surface runoff prior to disposal. The system capacity is flexible and able to handle multiple inputs from a variety of sources and particularly suited to applications where the influent is pumped.	
S3.4 (AEIAR-130/2009) and S5.8 (AEIAR-170/2013)	Open stockpiles of construction materials (for examples, aggregates, sand and fill material) of more than 50 m <sup>3</sup> should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.	٨
(************************************	Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.	Λ
S3.4 (AEIAR-130/2009)	Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecast, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events.	٨
	Oil interceptors should be provided in the drainage system and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain.	Λ
S3.4 (AEIAR-130/2009) and S5.8 (AEIAR-170/2013)	All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and located wheel washing bay should be provided at every site exit, and wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting	٨

EIA Ref.	Mitigation Measures	Status
	from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.	
S5.8 (AEIAR-170/2013)	Boring and Drilling Water Water used in ground boring and drilling for site investigation or rock / soil anchoring should as far as practicable be re-circulated after sedimentation. When there is a need for final disposal, the wastewater should be discharged into storm drains via silt removal facilities.	^
	Acid Cleaning, Etching and Pickling Wastewater Acidic wastewater generated from acid cleaning, etching, pickling and similar activities should be neutralized to within the pH range of 6 to 10 before discharging into foul sewers	^
S3.4	Drainage	
(AEIAR-130/2009)	It is recommended that on-site drainage system should be installed prior to the commencement of other construction activities. Sediment traps should be installed in order to minimise the sediment loading of the effluent prior to discharge into foul sewers. There should be no direct discharge of effluent from the site into the sea.	٨
S3.4 (AEIAR-130/2009)	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment control measures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage should be reinstated to its original condition when the construction work has finished or the temporary diversion is no longer required.	^

EIA Ref.	Mitigation Measures	Status
S3.4 (AEIAR-130/2009)	All fuel tanks and storage areas should be provided with locks and be located on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank, to prevent spilled fuel oils from reaching the coastal waters of the Victoria Harbour WCZ.	۸ 
S5.8 (AEIAR-170/2013)	There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. Minimum distance of 100 m should be maintained between the discharge points of construction site effluent and the existing seawater intakes and the planned WSR mentioned in S5.3.1 as appropriate. The beneficial uses of the treated effluent for other on-site activities such as dust suppression, wheel washing and general cleaning etc., can minimise water consumption and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the relevant WPCO licence which is under the ambit of regional office (RO) of EPD.	Λ
S3.4 (AEIAR-130/2009) and S5.8 (AEIAR-170/2013)	Sewage EffluentConstruction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage may need to be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets should be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor should also be responsible for waste disposal and maintenance practices.	٨
S5.8	Notices should be posted at conspicuous locations to remind the workers not to discharge	^

EIA Ref.	Mitigation Measures	Status
(AEIAR-170/2013)	any sewage or wastewater into the surrounding environment. Regular environmental audit of the construction site will provide an effective control of any malpractices and can encourage continual improvement of environmental performance on site. It is anticipated that sewage generation during the construction phase of the project would not cause water pollution problem after undertaking all required measures.	
S3.4 (AEIAR-130/2009) and S5.8 (AEIAR-170/2013)	<u>Stormwater Discharges</u> Minimum distances of 100 m should be maintained between the existing or planned stormwater discharges and the existing or planned seawater intakes.	^
	Debris and Litter In order to maintain water quality in acceptable conditions with regard to aesthetic quality, contractors should be required, under conditions of contract, to ensure that site management is optimised and that disposal of any solid materials, litter or wastes to marine waters does not occur.	٨
S5.8 (AEIAR-170/2013)	Accidental Spillage Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation, should be observed and complied with for control of chemical wastes. Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	^

EIA Ref.	Mitigation Measures	Status
	<ul> <li>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows:</li> <li>Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</li> <li>Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents.</li> <li>Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.</li> </ul>	∧ ∧ ∧
Construction Waste	Management	
S6.7 (AEIAR-170/2013)	Prepare a Waste Management Plan, which becomes a part of the Environmental Management Plan, in accordance with the requirements stipulated in ETWB TC (W) No. 19/2005, approved by the Engineer/Supervising Officer of the Project based on current practices on construction sites.	٨
S3.5 (AEIAR-130/2009) and S6.7 (AEIAR-170/2013)	<ul> <li>Good Site Practices</li> <li>It is not anticipated that adverse waste management related impacts would arise, provided that good site practices are adhered to. Recommendations for good site practices during construction activities include:</li> <li>Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site Training of site personnel in proper waste management and chemical waste handling procedures</li> </ul>	^
	Provision of sufficient waste disposal points and regular collection for disposal	۸

EIA Ref.	Mitigation Measures	Status
	• Appropriate measures to minimise windblown litter and dust during transportation of	^
	waste by either covering trucks or by transporting wastes in enclosed containers	
	<ul> <li>A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites)</li> </ul>	^
	<ul> <li>Regular cleaning and maintenance systems, sumps and oil interceptors</li> </ul>	$\wedge$
	<ul> <li>Separation of chemical wastes for special handling and appropriate treatment</li> </ul>	^
	• Separation of chemical wastes for special handling and appropriate treatment	
	Waste Reduction Measures	
	Good management and control can prevent the generation of a significant amount of	
	waste. Waste reduction is best achieved at the planning and design stage, as well as by	
	ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:	
	• Sort C&D waste from demolition of the remaining structures to recover recyclable portions such as metals	۸
	<ul> <li>Segregation and storage of different types of waste in different containers, skips or</li> </ul>	٨
	stockpiles to enhance reuse or recycling of materials and their proper disposal	
	<ul> <li>Encourage collection of aluminium cans, PET bottles and paper by providing separate</li> </ul>	^
	labelled bins to enable these wastes to be segregated from other general refuse generated by the work force	
	<ul> <li>Any unused chemicals or those with remaining functional capacity should be recycled</li> </ul>	Λ
	<ul> <li>Proper storage and site practices to minimise the potential for damage or</li> </ul>	Λ
	contamination of construction materials	
	<ul> <li>Plan and stock construction materials carefully to minimize amount of waste</li> </ul>	^
	generated and avoid unnecessary generation of waste	
	<ul> <li>Training should be provided to workers about the concepts of site cleanliness and</li> </ul>	٨
	appropriate waste management procedures, including waste reduction, reuse and	
	recycle.	

EIA Ref.	Mitigation Measures	Status
S3.5 (AEIAR-130/2009)	<ul> <li>Construction and Demolition Materials</li> <li>Mitigation measures and good site practices should be incorporated in the contract document to control potential environmental impact from handling and transportation of C&amp;D material. The mitigation measures include:</li> <li>Where it is unavoidable to have transient stockpiles of C&amp;D material within the Project work site pending collection for disposal, the transient stockpiles shall be</li> </ul>	Λ
	<ul> <li>located away from waterfront or storm drains as far as possible.</li> <li>Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric.</li> </ul>	٨
	<ul> <li>Skip hoist for material transport should be totally enclosed by impervious sheeting.</li> <li>Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site.</li> </ul>	л л
	<ul> <li>The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.</li> </ul>	^
	<ul> <li>The load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle.</li> </ul>	٨
	<ul> <li>All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet.</li> </ul>	٨
	• The height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading.	٨
	When delivering inert C&D material to public fill reception facilities, the material should consist entirely of inert construction waste and of size less than 250mm or other sizes as agreed with the Secretary of the Public Fill Committee. In order to monitor the disposal of the surplus C&D material at the designed public fill reception facility and to control fly tipping, a trip-ticket system as stipulated in the ETWB TCW No. 31/2004 "Trip Ticket	٨

EIA Ref.	Mitigation Measures	Status
	System for Disposal of Construction and Demolition Materials" should be included as one of the contractual requirement sand implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. An Independent Environmental Checker should be responsible for auditing the results of the system.	
S3.5 (AEIAR-130/2009)	General Refuse General refuse should be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Effective collection and storage methods (including enclosed and covered area) of site wastes would be required to prevent waste materials from being blown around by wind, wastewater discharge by flushing or leaching into the marine environment, or creating odour nuisance or pest and vermin problem	^
Construction Lands	cape and Visual	
\$3.8.12	• Minimized construction area and contractor's temporary works areas.	٨
(AEIAR-130/2009)	• All existing trees should be carefully protected during construction.	^
and S7.9 (AEIAR-170/2013)	• Trees unavoidably affected by the works should be transplanted where practical. Detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBC 2/2004 and 3/2006. Final locations of transplanted trees should be agreed prior to commencement of the work.	^
	• Control of night-time lighting.	٨
	<ul> <li>Erection of decorative screen hoarding.</li> </ul>	٨
	<ul> <li>Reduction of construction period to practical minimum.</li> </ul>	٨
	• Limitation of / Ensuring no run-off into surrounding landscape and adjacent seawater areas.	٨
	<ul> <li>Temporary or advance landscape should be provided along the temporary access roads to the Cruise Terminal until such time as road D3 is open.</li> </ul>	٨

Remarks:	EIA Report (AEIAR-130/2009) – Kai Tak Development						
	EIA Report (AEIAR-170/2013) – Kai Tak Development – Roads D3A & D4A						
	<ul> <li>Compliance of mitigation measure;</li> <li>N/A Not Applicable at this stage;</li> </ul>	X Non-compliance of mitigation measure;					
	N/A Not Applicable at this stage, N/A(1) Not observed;	• Non-compliance but rectified by the contractor;					
	* Recommendation was made during site audit but improved/rectified by the contractor.	# Recommendation was made during site audit but not yet improved/rectified by the contractor.					

APPENDIX F SUMMARIES OF ENVIRONMENTAL COMPLAINT, WARNING, SUMMON AND NOTIFICATION OF SUCCESSFUL PROSECUTION

## Contract No. KL/2014/01 Kai Tak Development –Stage 2 Infrastructure Works for Developments at the Southern Part of the Former Runway

Appendix F – Summary of environmental complaint, warning, summon and notification of successful prosecution

**Reporting Month**: March 2023

Contract No. KL/2014/01

Log Ref.	Location	Received Date	Details of Complaint/warning/summon and prosecution	Investigation/Mitigation Action	Status
N/A	N/A	N/A	N/A	N/A	N/A

**Remarks**: No environmental complaint/warning/summon and prosecution were received in the reporting period.

APPENDIX G WASTE GENERATED QUANTITY

## Appendix G. Monthly Summary Waste Flow Table

Name of Department: CEDD

Contract No KL/2014/01

Month	Actual Quantities of Inert C&D Materials Generated Monthly				Actual Quantities of C&D Wastes Generated Monthly						
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects *	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in tonne)	(in tonne)	(in tonne)	(in tonne)	(in tonne)	(in tonne)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in tonne)
Jan	110.01	0	0	0	82.86	0	0	0	0	0	27.15
Feb	54.19	0	0	0	6.43	0	0	0	0	0	47.76
Mar	23.57	0	0	0	6.66	0	0	0	0	0	16.91
Apr	0.00	0	0	0	0.00	0	0	0	0	0	0.00
May	0.00	0	0	0	0.00	0	0	0	0	0	0.00
June	0.00	0	0	0	0.00	0	0	0	0	0	0.00
Sub-total	187.77	0	0	0	0.00	0	0	0	0	0	91.82
July	0.00	0	0	0	0.00	0	0	0	0	0	0.00
Aug	0.00	0	0	0	0.00	0	0	0	0	0	0.00
Sept	0.00	0	0	0	0.00	0	0	0	0	0	0.00
Oct	0.00	0	0	0	0.00	0	0	0	0	0	0.00
Nov	0.00	0	0	0	0.00	0	0	0	0	0	0.00
Dec	0.00	0	0	0	0.00	0	0	0	0	0	0.00
Total	187.77	0	0	0	95.95	0	0	0	0	0	91.82

## Monthly Summary Waste Flow Table for 2023

\* Transfer to alterative disposal ground at Lung Kwu Sheung Tan EPD approved recycler
