

Lam Geotechnics Limited

Contract No. HK/2015/01 Wanchai Development Phase II and Central-Wanchai Bypass Sampling, Field Measurement and testing Works (Stage 3) Monthly EM&A Report (January 2019)

#### CONTRACT NO: HK/2015/01

#### WANCHAI DEVELOPMENT PHASE II AND CENTRAL WANCHAI BYPASS SAMPLING, FIELD MEASUREMENT AND TESTING WORKS (STAGE 3)

ENVIRONMENTAL PERMIT NO. EP-356/2009, FURTHER EVIRONMENTAL PERMIT NOS. FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009, FEP-07/356/2009 AND FEP-08/356/2009

#### MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT

- JANUARY 2019 -

CLIENTS:

Civil Engineering and Development Department

and

**Highways Department** 

#### PREPARED BY:

Lam Geotechnics Limited

11/F Centre Point 181-185 Gloucester Road, Wanchai, H.K.

Telephone: (852) 2882-3939 Facsimile: (852) 2882-3331 E-mail: <u>info@lamenviro.com</u> Website: <u>http://www.lamenviro.com</u>

**CERTIFIED BY:** 

Rayt

Raymond Dai Environmental Team Leader

DATE:

4 February 2019



Ref.: AACWBIECEM00\_0\_11051L.19

11 February 2019

By Post and Fax (3912 3010)

AECOM Asia Company Limited Engineer's Representative's Office 25 Hung Hing Road, Causeway Bay, Hong Kong

Attention: Mr. Peter Poon

Dear Mr. Poon,

## Re: Contract No. HK/2015/01 Wan Chai Development Phase II - Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3)

### Monthly Environmental Monitoring and Audit Report (January 2019) for EP-356/2009, FEP-02/356/2009, FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009, FEP-07/356/2009 and FEP-08/356/2009

Reference is made to the Environmental Team's submission of the captioned Monthly Environmental Monitoring and Audit (EM&A) Report for January 2019 received by email on 4 February 2019 for our review and comment.

Please be informed that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 in the captioned Environmental Permits.

Thank you very much for your kind attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,

David Yeung Independent Environmental Checker

Q:\Projects\AACWBIECEM00\Corr\AACWBIECEM00\_0\_11051L.19.docx

Ramboll Hong Kong Limited 英環香港有限公司

21/F, BEA Harbour View Centre, 56 Gloucester Road, Wan Chai, Hong Kong Tel: 852.3465 2888 Fax: 852.3465 2899 www.ramboll.com

Encl.		
C.c.		
HyD	Attn: Mr. Tony Cheung	by fax: 2714 5289
CEDD	Attn: Mr. Henry Tsang	by fax: 2301 1277
AECOM	Attn: Mr. Frankie Fan	by fax: 2691 2649
AECOM	Attn: Mr. Conrad Ng	by fax: 2691 2649
Lam	Attn: Mr. Raymond Dai	by fax: 2882 3331



Lam Geotechnics Limited

## TABLE OF CONTENTS

1	Ι	NTRODUCTION	9
	1.1 1.2	Scope of the Report Structure of the Report	
2	F	PROJECT BACKGROUND	.12
	2.1 2.2 2.3 2.4	Background Scope of the Project and Site Description Division of the Project Responsibility Project Organization and Contact Personnel	12 14
3	S	TATUS OF REGULATORY COMPLIANCE	. 19
	3.1	Status of Environmental Licensing and Permitting under the Project	19
4	MO	NITORING REQUIREMENTS	.30
	4.1 4.2 4.3	Noise Monitoring Air Monitoring Water Quality Monitoring	31
5.	MO	NITORING RESULTS	.41
	5.1 5.2 5.3 5.4	Noise Monitoring Results Air Monitoring Results Water quality monitoring Results Waste Monitoring Results	.43 .44
6.	CON	APLIANCE AUDIT	55
	6.1 6.2 6.3 6.4 6.5	Noise Monitoring Air Monitoring Water Quality Monitoring Review of the Reasons for and the Implications of Non-compliance Summary of action taken in the event of and follow-up on non-complia 56	55 55 56
7. PR		AULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT	. 57
8.	ENV	IRONMENTAL SITE AUDIT	. 58
9. (	COMP	LAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION	. 59
10.	CON	ICLUSION	61



#### LIST OF TABLES

Table I	Summary of Water Quality Monitoring Exceedances in Reporting Month
Table II	Summary of Enhanced Dissolved Oxygen Monitoring Exceedances in Reporting Month
Table 2.1	Schedule 2 Designated Projects under this Project
Table 2.2	Details of Individual Contracts under the Project
Table 2.3	Contact Details of Key Personnel
Table 3.1	Summary of the current status on licences and/or permits on environmental
	protection pertinent to the Project
Table 3.2	Cumulative Summary of Valid Licences and Permits under Contract no. HK/2009/01
Table 3.3	Summary of submission status under FEP-02/356/2009 Condition
Table 3.4	Cumulative Summary of Valid Licences and Permits under Contract no. HK/2009/02
Table 3.4	Summary of submission status under FEP-03/356/2009 Condition
Table 3.6	Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/15
Table 3.7	Summary of submission status under FEP-04/356/2009 Condition
Table 3.8	Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/19
Table 3.9	Cumulative Summary of Valid Licences and Permits under Contract no. HK/2012/08
Table 3.9	Summary of submission status under EP-356/2009 & FEP-06/356/2009 Condition
Table 3.10	Cumulative Summary of Valid Licences and Permits under Contract no. HY/2010/08
	Summary of submission status under EP-356/2009 and FEP-07/356/2009 Condition
Table 3.12	
Table 4.1	Noise Monitoring Station
Table 4.2	Air Monitoring Station Marine Water Quality Stations for Water Quality Manitoring
Table 4.3	Marine Water Quality Stations for Water Quality Monitoring
Table 4.4	Marine Water Quality Monitoring Frequency and Parameters
Table 4.5	Marine Water Quality Stations for Enhanced Water Quality Monitoring
Table 5.1	Noise Monitoring Station for Contract no. HK/2009/02
Table 5.2	Noise Monitoring Station for Contract no. HY/2009/15
Table 5.3	Noise Monitoring Station for Contract no. HY/2009/19
Table 5.4	Noise Monitoring Station for Contract no. HY/2010/08
Table 5.5	Air Monitoring Station for Contract no. HK/2009/01
Table 5.6	Air Monitoring Station for Contract no. HK/2009/02
Table 5.7	Air Monitoring Station for Contract no. HY/2009/15
Table 5.8	Air Monitoring Stations for Contract no. HY/2009/19
Table 5.9	Air Monitoring Stations for Contract no. HK/2012/08
	Air Monitoring Stations for Contract no. HY/2010/08
Table 5.11	Water quality monitoringStations for contracts with respect to remaining DP3 work
	areas after the completion of DP5 & DP6 in 2012 and intake diversion in 2013
Table 5.12	
Table 5.13	Water quality monitoringStations for Contract no. HK/2009/02
Table 5.14	
	Water quality monitoring Station for Contract no. HY/2010/08
	Enhance Dissolved Oxygen Monitoring Stations for Contract no. HY/2010/08
	Details of Waste Disposal for Contract no. HK/2009/01
	Details of Waste Disposal for Contract no. HK/2009/02
Table 5.19	
Table 5.20	Details of Waste Disposal for Contract no. HY/2009/19
Table 5.21	Details of Waste Disposal for Contract no. HK/2012/08
Table 5.22	Details of Waste Disposal for Contract no. HY/2010/08
Table 8.2	Summary of Environmental Inspections for Contract no. HK/2009/02
Table 8.3	Summary of Environmental Inspections for Contract no. HY/2009/19
Table 8.5	Summary of Environmental Inspections for Contract no. HK/2012/08
Table 8.6	Summary of Environmental Inspections for Contract no. HY/2010/08
Table 9.1	Cumulative Statistics on Complaints
Table 9.2	Cumulative Statistics on Successful Prosecutions
Table 10.1	Construction Activities and Recommended Mitigation Measures in Coming
	Reporting Month



#### **LIST OF FIGURES**

- Figure 2.1 **Project Layout**
- **Project Organization Chart** Figure 2.2
- Figure 4.1 Locations of Environmental Monitoring Stations

#### LIST OF APPENDICES

- Appendix 3.1 Environmental Mitigation Implementation Schedule
- Appendix 4.1 Action and Limit Level
- Appendix 4.2 Copies of Calibration Certificates
- Appendix 5.1 Monitoring Schedule for Reporting Month and Coming month
- **Noise Monitoring Results and Graphical Presentations** Appendix 5.2
- Appendix 5.3 Air Quality Monitoring Results and Graphical Presentations
- Appendix 5.4 Water Quality Monitoring Results and Graphical Presentations
- Appendix 6.1 Event Action Plans
- Appendix 6.2Summary for Notification of ExceedanceAppendix 9.1Complaint Log
- Appendix 10.1 Construction Programme of Individual Contracts



Lam Geotechnics Limited

#### EXECUTIVE SUMMARY

- This is the Environmental Monitoring and Audit (EM&A) Monthly Report January 2019 for the Project of Wan Chai Development Phase II and Central-Wanchai Bypass under Environmental Permit no. EP-356/2009 and Further Environmental permit nos. FEP-02/356/2009, FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009, FEP-07/356/2009 and FEP-08/356/2009. This report presents the environmental monitoring findings and information recorded during the period of 27 December 2018 to 26 January 2019. The cut-off date of reporting is at 26<sup>th</sup> of each reporting month.
- ii. In the reporting month, the principal work activities of individual contracts conducted are as follow:

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East</u>

• Trimming of seabed profile at TWCR4

Contract no. HY/2009/19- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

• Seawall block reinstatement near box culvert T1

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> <u>Wan Chai West</u>

• Nil

Contract no. HY/2010/08 – Central - Wan Chai Bypass (CWB) – Tunnel (Slip Road 8)

Nil

### Noise Monitoring

- With respect to the shift in major construction site portions at Wan Chai North, the noise monitoring station M1a – Harbour Sports Centre was finely adjusted from East of Harbour Road Sports Centre to West of Harbour Road Sports Centre on 21 June 2016.
- With respect to the demolition of Ex-Harbour Road Sports Centre, the respective noise monitoring station M1a – Harbour Road Sports Centre were finely adjusted on 16 and 25 May 2017 and thereafter to the Footbridge for Harbour Road Sports for noise monitoring.
- v. Two limit level exceedance was recorded at M6 Hong Kong Baptist Church Henrietta Secondary School on 18 and 25 January 2019 in the reporting period. After the investigation, the exceedance was concluded as non-Project related.
- vi. Noise monitoring during daytime and restricted hour were conducted at the stations M1a, M4b, M5b and M6 on a weekly basis in the reporting month.



#### Air Quality Monitoring

- vii. No action or limit level exceedance was recorded in the reporting period.
- viii. With respect to the proposed demolition of the Oil Street Site Office, the respective air quality monitoring station CMA1b – Oil Street Site Office was finely adjusted from the Oil Street Site Office to Harbour Grand Hotel Boundary Wall from 05 June 2017 onwards.
- ix. With respect to the proposed demolition of eastern podium of Oil Street Site Office, the respective air quality monitoring station CMA1b – Oil Street Site Office was finely adjusted from East podium of the Oil Street Site Office to the West podium of the Oil Street Site Office on 21 December 2016.
- x. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted at CMA1b – Oil Street Site Office; CMA2a – Causeway Bay Community Center; CMA3a – CWB
   PRE Site Office Area; CMA4a – Society for the Prevention of Cruelty to Animals; CMA5b – Pedestrian Plaza; CMA6a – WDII PRE Site Office in the reporting month.

#### Water Quality Monitoring

- xi. Action and Limit level of water quality monitoring was transited from wet season to dry season from 01 October 2018.
- xii. With respect to the reinstatement of the silt screen system for Cooling Water Intakes P7, P8, P9 and WSD Water Intake RW21, the respective water quality monitoring was reverted to the previous monitoring location for Water Quality Monitoring Station RW21-P789 from water quality stations RW21-P789 East (RW21-P789E) and RW21-P789 West (RW21-P789W) from 25 January 2017 onwards.
- xiii. With respect to the removal of silt screen at WQM station RW21-P789 on 26 November 2016, the respective water quality monitoring at RW21-P789 was adjusted to RW21-P789E and RW21-P789W since 28 November 2016 ebb-tide.
- xiv. With respect to the temporarily suspension of marine construction works at WCR3 Area by Contract HK/2009/02, the installed silt screen for intake group (P7, P8, P9 and WSD21) was removed on 26 November 2016.
- As advised by the Contractor of HK/2009/01, all silt screen remains removal works at P1, P3,
   P4, P5 and C1 water quality monitoring stations were completed on 8 May 2016.
- xvi. With respect to the marine works undertaken at WCR3 by Contract HK/2009/02, the respective water quality monitoring station C1 associated with Contract HK/2009/01 was updated as in association with Contract HK/2009/01 and Contract HK/2009/02.
- xvii. With respect to the marine works undertaken at CBTS by Contract HY/2010/08, the respective water quality monitoring station C7 associated with Contract HY/2009/15 was updated as in association with Contract HY/2009/15 and Contract HY/2010/08.



- xviii. With respect to the marine works undertaken at HKCEC2 by Contract HK/2012/08, the respective water quality monitoring station WSD19, P1, P3, P4, and P5 were associated with Contract HK/2012/08.
- xix. As confirmed by WDII RSS, the marine construction works under Contract HK/2009/01 have been completed since 24 July 2017, the monitoring association with Contract HK/2009/01 and relevant reporting has been ceased in the reporting month.
- xx. Enhanced DO monitoring at Windsor House Cooling (Station Ref: C7) was temporarily suspended since 22 October 2014 with respect to the formation of temporary reclamation zone TS3
- xxi. Referring to CWB RSS confirmation on the completion of marine construction activities within the Ex-PCWA area and the completion of the post construction water quality monitoring, the respective Enhance DO Monitoring within Ex-PCWA for monitoring station Ex-PCWA SE and Ex-PCWA SW was temporarily suspended since 07 March 2017 ebb tide onwards.
- xxii. Water quality monitoring station C7 and Enhance DO monitoring station C6 shall be associated with Contract HY/2010/08, upon confirmation of marine construction works completion under Contract HY/2009/15 at CBTS area and Ex-PCWA area since 19 June 2017.
- xxiii. Enhanced DO monitoring at Windsor House Cooling (Station Ref: C7) was resumed from 1
   February 2018 onwards with respect to the completion of removal of temporary reclamation zone.
- xxiv. Referring to CWB RSS confirmation on the completion of removal of temporary reclamation within the TS3 area and the completion of the post construction water quality monitoring, the respective Enhance DO Monitoring within TS3 for monitoring station C6 and C7 was temporarily suspended since 05 March 2018 onwards.
- xxv. Referring to CWB RSS confirmation on the completion of marine works within the TS3 area and the completion of the post construction water quality monitoring, the respective water quality monitoring within TS3 for monitoring station C7 was temporarily suspended since 29 October 2018 onwards.
- xxvi. Referring to WDII RSS confirmation on the completion of marine works under HK/2012/08 within the EP-356 area on 2 January 2019, the four weeks post-construction monitoring for respective water quality monitoring stations P1, P3, P4, P5 and WSD19 within EP-356 area was started on 2 January 2019.



		Mid-flood				Mid-ebb							
Contract no.	monitoring	D	0	Turb	idity	S	S	D	0	Turb	oidity	S	S
	Station	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL
HK/2009/02	C1	0	0	0	0	0	0	0	0	0	0	0	0
	WSD19	0	0	0	0	0	0	0	0	0	0	0	0
	P1	0	0	0	0	0	0	0	0	0	0	0	0
HK/2012/08	P3	0	0	0	0	0	0	0	0	0	0	0	0
	P4	0	0	0	0	0	0	0	0	0	0	0	0
	P5	0	0	0	0	1	0	0	0	0	0	0	0
HK/2009/02	RW21-P789	0	0	0	0	0	0	0	0	0	0	0	0
То	tal	0	0	0	0	1	0	0	0	0	0	0	0

#### Table I Summary of Water Quality Monitoring Exceedances in Reporting Month

Remarks:

- 1. The cessation of seawater intake operation for C6 was confirmed on 17 May 2011 and the water quality monitoring at C6 was then terminated since 17 May 2011.
- 4-week post construction water quality monitoring at WSD9, WSD10, WSD15 and WSD17 were completed on 6 Feb 2012 and the water quality monitoring at WSD 10 and WSD15 were temporary suspended since 8 Feb 2012, and WSD9 and WSD17 was implemented with respect to HK/2009/02 from 8 Feb 2012 onwards.
- 3. C8 and C9 were implemented with respect to HY/2009/19 from 28 Jan 2012.
- 4. C8 & C9 were temporary suspended since 4 March 2013.
- 5. WSD7 and WSD20 water quality monitoring were temporarily suspended from 27 Apr 2012.
- 6. C2, C3 C4e and C4w water quality monitoring station was temporarily suspended since 22 Apr 2013
- 7. P1, P3, P4 and P5 were commenced since 24 Apr 2013
- 8. C5e and C5w water quality monitoring station was temporarily suspended since 29 Jul 2013.
- 9. WSD21 water quality monitoring station was temporarily suspended since 12 Mar 2014
- 10. WSD9 and WSD17 water quality monitoring station was temporarily suspended since 8 Sep 2014 flood tide.
- 11. The water quality monitoring station C1 shall be associated with Contract No. HK/2009/02 upon commencement of marine works under DP3 at WCR3 area.
- The water quality monitoring station RW21-P789 was adjusted to RW21-P789E and RW21-P789W since 28 November 2016 ebb-tide.
- The water quality monitoring was reverted to previous monitoring station RW21-P789 from PW21-P789E and RW21-P789W from 25 January 2017 onwards.
- xxvii. One action level exceedance of suspended solids was recorded on 25 January 2019 at P5 in the reporting period. After the investigation, the exceedance was concluded as non-project related.



#### Complaints, Notifications of Summons and Successful Prosecutions

xxviii. One environmental complaint was received in the reporting period.

An EPD complaint was referred to the ET on 16 January 2019 (CASE Ref: H08/RS/00001488-19, H08/RS/00001532-19, and H08/RS/00001663-19). The complainant reported that milky water discharge was found at the Victoria Harbour, near Causeway Bay Typhoon Shelter on 12 January 2019.

ET confirmed with the WDII Resident Site Staff that the concerned area was located out of the site area of Contract No. HK/2009/02 and the Contractor of HK/2009/02 had no activity at the area concerned on 12 January 2019.

ET confirmed with the CWB Resident Site Staff that no construction works was conducted by the contractor of HY/2010/08 at Victoria Harbour, near Causeway Bay Typhoon Shelter on 12 January 2019 at around noon.

Despite no construction activity was conducted under Contract HK/2009/02 and HY/2010/08 on the concerned date and location as confirmed with corresponding Resident Site Staff, in view of public concern, the Contractor of Contract HK/2009/02 and HY/2010/08 were reminded to review the on-site drainage system and the operation of wastewater treatment system. The Contractor of Contract HK/2009/02 and HY/2010/08 were also reminded to provide mitigation measure such as deployment of silt curtain to enclose the works area if any marine activity to be conducted at the concerned area.

#### Site Inspections and Audit

xxix. The Environmental Team (ET) conducted weekly site inspections for Contract nos. HK/2009/02, HY/2009/19, HK/2012/08 and HY/2010/08 under EP no. EP-356/2009 in the reporting month. Major observations and recommendations made during the audit sessions were rectified by the Contractors. No non-conformance was identified during the site inspections.



Future Key Issues

xxx. In coming reporting month, the principal work activities of individual contracts are anticipated as follows:

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East</u>

• Placing rock armour at TWCR4

Contract no. HY/2009/19- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

• Seawall block reinstatement near box culvert T1

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> <u>Wan Chai West</u>

• Nil

Contract no. HY/2010/08 - Central - Wan Chai Bypass (CWB) - Tunnel (Slip Road 8)

• Nil



#### 1 Introduction

#### 1.1 Scope of the Report

- 1.1.1. Lam Geotechnics Limited (LGL) has been appointed to work as the Environmental Team (ET) under Environmental Permit no. EP-356/2009 and Further Environmental permit nos. FEP-02/356/2009, FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009, FEP-07/356/2009 and FEP-08/356/2009 to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) and in the EM&A Manual of the approved EIA Report for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001).
- 1.1.2. This report presents the environmental monitoring and auditing work carried out in accordance to the Section 10.3 of EM&A Manual and "*Environmental Monitoring and Audit Requirements*" under Particular Specification Section 27.
- 1.1.3. This report documents the finding of EM&A works for Environmental Permit no. EP-356/2009, Further Environmental Permit no. FEP-02/356/2009, FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009, FEP-07/356/2009 and FEP-08/356/2009 during the period of 27 December 2018 to 26 January 2019. The cut-off date of reporting is at 26<sup>th</sup> of each reporting month.



Lam Geotechnics Limited

## 1.2 Structure of the Report

- **Section 1** *Introduction* details the scope and structure of the report.
- Section 2 *Project Background* summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.
- Section 3 Status of Regulatory Compliance summarizes the status of valid Environmental Permits / Licenses during the reporting period.
- Section 4 *Monitoring Requirements* summarizes all monitoring parameters, monitoring methodology and equipment, monitoring locations, monitoring frequency, criteria and respective event and action plan and monitoring programmes.
- Section 5 *Monitoring Results* summarizes the monitoring results obtained in the reporting period.
- Section 6 Compliance Audit summarizes the auditing of monitoring results, all exceedances environmental parameters.
- Section 7 *Cumulative Construction Impact due to the Concurrent Projects* summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.
- Section 8 Environmental Site Audit summarizes the findings of weekly site inspections undertaken within the reporting period, with a review of any relevant follow-up actions within the reporting period.
- Section 9Complaints, Notification of summons and Prosecution summarizes the<br/>cumulative statistics on complaints, notification of summons and prosecution
- Section 10 Conclusion



## 2 Project Background

### 2.1 Background

- 2.1.1. "Wan Chai Development phase II and Central-Wan Chai Bypass" and "Central-Wan Chai Bypass and Island Eastern Corridor Link" (hereafter called "the Project") are Designed Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Reports for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001) and Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) have been approved on 31 August 2001 and 11 December 2008 respectively.
- 2.1.2. The key purpose of Wan Chai Development Phase II (WDII) is to provide land at Wan Chai North and North Point for construction of the Central-Wan Chai Bypass and Island Eastern Corridor Link (CWB). Land formed under the project will be developed as a world-class waterfront promenade joining that at the new Central waterfront for public enjoyment.
- 2.1.3. There is a compelling and present need for the CWB to provide relief to the very congested east-west Connaught Road Central/Harcourt Road / Gloucester Road Corridor (the Corridor) which is currently operating beyond its capacity. The CWB will provide relief to the existing congestion along the Corridor and cater for the anticipated growth of traffic on Hong Kong Island. Without the CWB and its access roads, there will not be sufficient capacity to serve the heavy traffic demands at both strategic and local levels.

### 2.2 Scope of the Project and Site Description

- 2.2.1. The Project is located mainly in Wan Chai North, Causeway Bay and North Point, and is demarcated by Gloucester Road and Victoria Park Road to the south, Fenwick Pier Street to the west and Tong Shui Road Interchange to the east, as shown in *Figure 2.1*.
- 2.2.2. The study area encompasses existing developments along the Wan Chai, Causeway Bay and North Point shorelines. Major land uses include the Hong Kong Convention & Exhibition Centre (HKCEC) Extension, the Wan Chai Ferry Pier, the ex-Wan Chai Public Cargo Working Area (ex-PCWA), the Royal Hong Kong Yacht Club (RHKYC), the Police Officers' Club, the Causeway Bay Typhoon Shelter (CBTS) and commercial and residential developments.
- 2.2.3. The scope of the Project comprises:
  - Land formation for key transport infrastructure and facilities, including the Trunk Road (i.e. CWB) and the associated slip roads for connection to the Trunk Road and for through traffic from Central to Wan Chai and Causeway Bay. The land formed for the above transport infrastructure will provide opportunities for the development of an attractive waterfront promenade for the enjoyment of the public



Lam Geotechnics Limited

- Reprovisioning / protection of the existing facilities and structures affected by the land formation works mentioned above
- Extension, modification, reprovisioning or protection of existing storm water drainage outfalls, sewerage outfalls and watermains affected by the revised land use and land formation works mentioned above
- Upgrading of hinterland storm water drainage system and sewerage system, which would be rendered insufficient by the land formation works mentioned above
- Provision of the ground level roads, flyovers, footbridges, necessary transport facilities and the associated utility services
- Construction of the new waterfront promenade, landscape works and the associated utility services
- The Trunk Road (i.e. CWB) within the study area and the associated slip roads for connection to the Trunk Road.
- 2.2.4. The project also contains various Schedule 2 DPs that, under the EIAO, require Environmental Permits (Eps) to be granted by the DEP before they may be either constructed or operated. *Table 2.1* summarises the five individual DPs under this Project. *Figure 2.1* shows the locations of these Schedule 2 DPs.

ltem	Designated Project	EIAO Reference	Reason for inclusion
DP1	Central-Wanchai Bypass (CWB) including its road tunnel and slip roads	Schedule 2, Part I, A.1 and A.7	Trunk road and road tunnel more than 800 m in length
DP2	Road P2 and other roads which are classified as primary/district distributor roads	Schedule 2, Part I, A.1	Primary / district distributor roads
DP3	Reclamation works including associated dredging works	Schedule 2, Part I, C.1 and C.12	Reclamation more than 5 ha in size and a dredging operation less than 100 m from a seawater intake point
DP5	Wan Chai East Sewage Outfall	Schedule 2, Part I, F.5 and F.6	Submarine sewage pipelines with a total diameter more than 1,200 mm and include a submarine sewage outfall
DP6	Dredging for the Cross-harbour Water Mains from Wan Chai to Tsim Sha Tsui	Schedule 2, Part I, C.12	A dredging operation less than 100 m from a seawater intake point

 Table 2.1
 Schedule 2 Designated Projects under this Project



## 2.3 Division of the Project Responsibility

- 2.3.1. Due to the multi-contract nature of the Project, there are a number of contracts sub-dividing the whole works area into different work areas to be commenced. Contractors of individual contracts will be required by the EP holder to apply Further Environmental Permits (FEP) such that the impact monitoring stations are sub-divided accordingly to facilitate the implementation of EM&A programme and to streamline the EM&A reporting for individual FEP holders correspondingly.
- 2.3.2. The details of individual contracts are summarized in Table 2.2.

Contract No.	Contract Title	Associated DP(s)	Construction Commencement Date
HK/2009/01	Wan Chai Development Phase II – Central –Wanchai Bypass at Hong Kong	DP3, DP6	23 July 2010 (Completed)
	Convention and Exhibition Centre	DP1, DP2	25 August 2011 (Completed)
HK/2009/02	Wan Chai Development Phase II – Central –	DP3, DP5	5 July 2010
	Wan Chai Bypass at WanChai East	DP1	26 April 2011
HY/2009/11	Wan Chai Development Phase II and Central – Wan Chai Bypass – North Point Reclamation	DP3	17 March 2010 (Completed)
HY/2009/15	Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)	DP3	10 November 2010 (Completed)
		DP1	13 July 2011 (Completed)
HK/2010/06	Wan Chai Development Phase II-Central-Wan Chai Bypass over MTR Tsuen Wan Line	DP3	22 March 2011 (Completed)
04/HY/2006	Reconstruction of Bus Terminus near Man Yiu Street and Man Kwong Street	DP1	September 2010 (Completed)
HY/2009/17	Central – Wan Chai Bypass (CWB) at FEHD Whitfield Depot – Advanced piling works.	DP1	5 October 2010 (Completed)
HY/2009/18	Central – Wan Chai Bypass (CWB) – Central Interchange	DP1	21 April 2011 (Completed)
HY/2009/19	Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link	DP1	24 March 2011

#### Table 2.2 Details of Individual Contracts under the Project



Contract No.	Contract Title	Associated DP(s)	Construction Commencement Date
HK/2012/08	Wan Chai Development Phase II Central- Wan Chai Bypass at Wan Chai West	DP1,DP2, DP3	10 March 2014
HY/2010/08	Central- Wanchai Bypass Tunnel – Tunnel (Slip Road 8)	DP1, DP2, DP3	21 March 2013
HY/2011/08	Central-Wan Chai Bypass (CWB) – Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning	DP1	8 October 2014



## 2.4 Project Organization and Contact Personnel

- 2.4.1. Civil Engineering and Development Department and Highways Department are the overall project controllers for the Wan Chai Development Phase II and Central-Wan Chai Bypass respectively. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.4.2. The proposed project organization and lines of communication with respect to environmental protection works are shown in *Figure 2.2.* Key personnel and contact particulars are summarized in *Table 2.3*:

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Chief Resident Engineer	Ms. Gloria Tang	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3912 3388	3912 3328
Chun Wo – CRGL Joint Venture	Contractor under Contract no. HK/2009/02	Project Manager Quality & Environmental Manager	Mr. Paul Yu Mr. C.P. Ho	3658 3085 9191 8856	2827 9996
China State Construction	Contractor under Contract no.	Project Director	Mr. Chris Leung Mr. Patrick Ho	3557 6393 3557 6405	2566 2192
Engineering (HK) Ltd.	ering HY/2009/15	Site Agent Construction Manager	Mr. Tom Tong	3557 6415	
		Environmental Officer	Mr. Gabriel Wong	6114 9590	
		Environmental Supervisor	Mr. Gordon Lai	6145 6365	
Chun Wo –	Contractor under	Project Manager	Mr. David Lau	3758 8879	3757 8901
CRGL – MBEC_Joint	Contract no. HY/2009/19	Site Agent	Mr. William Luk	3758 6868	
Venture		Deputy Site Agent	Mr. Andy Chan	9879 4325	

### Table 2.3 Contact Details of Key Personnel



Party	Role	Post	Name	Contact No.	Contact Fax
		Environmental Manager / Environmental Officer	Mr. M.H. Isa	9884 0810	
		Assist Environmental Officer	Mr. James Chan	9602 2911	
		Construction Manager (Marine)	Mr. Wingo Wong	9300 2625	
		Construction Manager (Land)	Mr. Mark Mak	9356 4421	
		Construction Manager (Ext. Works)	Mr. Paul Wan	6629 4652	
		Construction Manager (Land)	Mr. Yung Kwok Wah	9834 1010	
China State-	Contractor under	Project Director	Mr. C. N. Lai	9106 5806	2877 1522
Build King Joint Venture	Contract no. HK/2012/08	Site Agent	Mr. George Cheung	9268 1918	
		Environmental Officer	Mr. James Ma	9130 9549	
		Environmental Supervisor	Mr. Y. L. Ho	9856 5669	
China State	Contractor under	Project Director	Mr. Chris Leung	3467 4299	2566 8061
	Contract no. HY/2010/08	Project Manager	Mr. Chan Ying Lun	3418 3001	
		Site Agent	Mr. Thomas Lui	3557 6452	
		Marine Manager	Mr. Nickael Chan	3557 6333	
		Construction Manager	Mr. Tom Tong	3557 6367	
		Environmental Officer	Mr. Gabriel Wong	3557 6466	



Party	Role	Post	Name	Contact No.	Contact Fax
Ramboll Hong	Independent	Independent	Mr. David Yeung	3465 2888	3465 2899
Kong Limited	Environmental	Environmental			
	Checker (IEC)	Checker (IEC)			
Lam	Environmental	Environmental	Mr. Raymond Dai	2882 3939	2882 3331
Geotechnics	Team (ET)	Team Leader			
Limited		(ETL)			

2.4.3. In the reporting month, the principal work activities of individual contracts conducted are as follow:

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East</u>

• Trimming of seabed profile at TWCR4

Contract no. HY/2009/19- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

Seawall block reinstatement near box culvert T1

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> Wan Chai West

• Nil

Contract no. HY/2010/08 - Central - Wan Chai Bypass (CWB) - Tunnel (Slip Road 8)

- Nil
- 2.4.4. In coming reporting month, the principal work activities of individual contracts are anticipated as follows:

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East</u>

• Placing rock armour at TWCR4

Contract no. HY/2009/19- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

• Seawall block reinstatement near box culvert T1

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> <u>Wan Chai West</u>

• Nil

Contract no. HY/2010/08 – Central - Wan Chai Bypass (CWB) – Tunnel (Slip Road 8)

Nil



## 3 Status of Regulatory Compliance

### 3.1 Status of Environmental Licensing and Permitting under the Project

3.1.1. A summary of the current status on licences and/or permits on environmental protection pertinent to the Project is shown in *Table 3.1*.

# Table 3.1 Summary of the current status on licences and/or permits on environmentalprotection pertinent to the Project

Permits and/or Licences	Reference No.	Issued Date	Status
Environmental Permit	EP-356/2009	30 Jul 2009	Valid
Environmental Permit	EP-364/2009/E	22 Dec 2016	Valid
Environmental Permit	EP-376/2009	13 Nov 2010	Valid
Further Environmental Permit	FEP-01/356/2009	18 Feb 2010	Surrendered
Further Environmental Permit	FEP-02/356/2009	24 Mar 2010	Surrendered
Further Environmental Permit	FEP-03/356/2009	24 Mar 2010	Valid
Further Environmental Permit	FEP-04/356/2009	22 Nov 2010	Valid
Further Environmental Permit	FEP-05/356/2009	24 Mar 2011	Surrendered
Further Environmental Permit	FEP-01/364/2009	24 Mar 2010	Valid
Further Environmental Permit	FEP-02/364/2009	21 Apr 2010	Valid
Further Environmental Permit	FEP-03/364/2009	12 Jul 2010	Surrendered
Further Environmental Permit	FEP-04/364/2009/A	14 Oct 2010	Surrendered
Further Environmental Permit	FEP-05/364/2009/A	15 Nov 2010	Valid
Further Environmental Permit	FEP-06/364/2009/A	22 Nov 2010	Valid
Further Environmental Permit	FEP-07/364/2009/B	20 Sep 2012	Surrendered
Further Environmental Permit	FEP-07/364/2009/D	24 Nov 2015	Valid
Further Environmental Permit	FEP-08/364/2009/A	15 Jun 2012	Surrendered
Further Environmental Permit	FEP-06/356/2009	5 Mar 2013	Valid



Permits and/or Licences	Reference No.	Issued Date	Status
Further Environmental Permit	FEP-07/356/2009	26 July 2013	Valid
Further Environmental Permit	FEP-09/364/2009/B	5 March 2013	Valid
Further Environmental Permit	FEP-10/364/2009/B	26 July 2013	Valid
Further Environmental Permit	FEP-08/356/2009	1 Aug 2016	Valid
Further Environmental Permit	FEP-11/364/2009/E	22 Dec 2016	Valid



3.1.2. Due to the multi-contract nature of the Project, the status of permits and/or licences under the individual contract(s) are presented as below:

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>WanChai East</u>

3.1.3. Summary of the current status on licences and/or permits on environmental protection pertinent and submission for contract no. HK/2009/02 under FEP-03/356/2009 are shown in *Table 3.4* and *Table 3.5*.

# Table 3.4 Cumulative Summary of Valid Licences and Permits under Contract no.HK/2009/02

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental	FEP-03/356/2009	24 Mar 2010	N/A	Valid
Permit	FEP-01/364/2009	24 Mar 2010	N/A	Valid
Notification of Works Under APCO	313962	2 Feb 2010	N/A	Valid
	GW-RS0713-18	14 Aug 2018	16 Aug 2018 to 14 Feb 2019	Valid
Construction Noise Permit (CNP) for non-piling	GW-RS0880-18	24 Sep 2018	26 Sep 2018 to 24 Mar 2019	Valid
equipment	GW-RS0931-18	16 Oct 2018	22 Oct 2018 to 18 Apr 2019	Valid
	GW-RS1281-18	8 Jan 2019	10 Jan 2019 to 8 Jul 2019	Valid
	GW-RS1253-18	8 Jan 2019	12 Jan 2019 to 31 Mar 2019	Valid
Discharge Licence	WT00022295-2015	12 Aug 2015	31 July 2020	Valid
	WT00025276-2016	19 Sep 2016	31 July 2021	Valid
Billing Account under Waste Disposal Ordinance (Land)	7010255	10 Feb 2010	N/A	Valid
Billing Account under Waste Disposal Ordinance (Marine)	7011496	6 Oct 2010	N/A	Valid
Registration as Chemical Waste Producer (Wan Chai)	WPN5213-135-C3593-01	10 Mar 2010	N/A	Valid
Registration as Chemical Waste Producer (TKO 137)	WPN5213-839-C3593-02	22 Sep 2010	N/A	Valid



EP Condition	Submission	Date of Submission
Condition 1.12	Commencement Date of Construction of Marine Works	8 April 2010
Condition 2.6	Management Organization of Main Construction Companies	10 April 2010
Condition 2.7	Works Schedule and Location Plans	8 April 2010
Condition 2.8	Silt Curtain Deployment Plan (Revision O)	24 May 2018
	Silt Screen Deployment Plan	21 April 2010
Condition 2.9	Supplementary Information for Existing WSD Salt Water Intakes at Quarry Bay and Sai Wan Ho	5 Oct 2010
	Silt Screen Deployment Plan (Revision F)	23 Nov 2016
Condition 2.17	Noise Management Plan	6 May 2010
	Landscape Plan (Decorative Screen Hoarding)	11 May 2010
Condition 2.18	Landscape Plan (Control of Night Time Lighting)	2 June 2010
	Landscape Plan (Combined Version)	20 July 2011
	Landscape Plan (Combined Version)	5 Aug 2011
	Acknowledge of Submission	22 Aug 2011

## Table 3.5 Summary of submission status under FEP-03/356/2009 Condition



<u>Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter</u> <u>Section)</u>

3.1.4. Summary of the current status on licences and/or permits on environmental protection pertinent and submission for contract no. HY/2009/15 under FEP-04/356/2009 are shown in *Table 3.6* and *Table 3.7*.

# Table 3.6 Cumulative Summary of Valid Licences and Permits under Contract no.HY/2009/15

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-04/356/2009	22 Nov 2010	N/A	Valid
Notification of Works Under APCO	321822	24 Sep 2010	N/A	Valid
Registration as a Chemical Waste Producer	WPN5213-147-C1169-35	15 Nov 2010	N/A	Valid
Billing Account under Waste Disposal Ordinance	7011553	30 Sep 2010	N/A	Valid



FEP Condition	Submission	Date of Submission
		300111551011
Condition 2.6	Management Organization of Main	30 Sep 2010
	Construction Companies	
	Amendment for Management Organization	16 May 2011
	of Main Construction Companies	
Condition 2.7	Works Schedule and Location Plans	27 Oct 2010
	Amendment for Works Schedule and	12 Nov 2010
	Location Plans	
Condition 2.8	Silt Curtain Deployment Plan	30 Nov 2010
	Amendment for Silt Curtain Deployment	24 Feb 2011
	Plan	
	Amendment for Silt Curtain Deployment	11 May 2011
	Plan	
	Amendment for Silt Curtain Deployment	11 Sep 2012
	Plan	
	Amendment for Silt Curtain Deployment	30 Oct 2012
	Plan	
Condition 2.9	Silt Screen Deployment Plan	19 Oct 2010
	Amendment for Silt Screen Deployment	18 Feb 2011
	Plan	
	Amendment for Silt Screen Deployment	15 Jun 2011
	Plan	
Condition 2.18	Proposal for the Removal of Odorous	13 Jan 2011
	Sediment and Slime	
	Amendment for Proposal for the Removal	8 Mar 2011
	of Odorous Sediment and Slime	
	Amendment for Proposal for the Removal	2 Aug 2011
	of Odorous Sediment and Slime	
Condition 2.21	Landscape Plan	18 Feb 2011
Condition 2.23	Noise Management Plan	20 Oct 2010
	Amendment for Noise Management Plan	27 Jan 2011

## Table 3.7 Summary of submission status under FEP-04/356/2009 Condition



<u>Contract no. HY/2009/19 – Central- Wan Chai Bypass Tunnel (North Point Section) and Island</u> <u>Eastern Corridor Link</u>

3.1.5. Summary of the current status on licences and/or permits on environmental protection pertinent for contract no. HY/2009/19 is shown in *Table 3.8* 

# Table 3.8 Cumulative Summary of Valid Licences and Permits under Contract no.HY/2009/19

Permit / Licence / Notification / Approval	Reference No.	Issued Date	Valid Period / Expiry date	Status
Further Environmental Permit	FEP-07/364/2009/D	24 Nov 2015	N/A	Valid
Notification of Works Under APCO	326160	24 Jan 2011	N/A	Valid
Notification of Works (further proposed change to the particulars) Under APCO	415587	11 Apr 2017	N/A	Valid
Construction Noise Permit (CNP) for piling equipment	-	-	-	-
Construction Noise Permit (CNP) (IEC Road Modification for Middle Section)	GW-RS1196-18	18 Dec 2018	22 Dec 2018 to 30 Apr 2019	Valid
Construction Noise Permit (CNP) (IEC Road Modification for Middle Section)	GW-RS1197-18	18 Dec 2018	22 Dec 2018 to 30 Apr 2019	Valid
Construction Noise Permit (CNP) (For CWB Commissioning)	GW-RS1201-18	18 Dec 2018	22 Dec 2018 to 31 Mar 2019	Valid
Construction Noise Permit (CNP) (IEC Road Modification for Middle Section)	GW-RS0016-19	16 Jan 2019	18 Jan 2019 to 30 Apr 2019	Valid
Construction Noise Permit (CNP) (For IEC Westbound)	GW-RS0014-19	16 Jan 2019	18 Jan 2019 to 30 Apr 2019	Valid



Permit / Licence / Notification / Approval	Reference No.	Issued Date	Valid Period / Expiry date	Status
C&D Waste Disposal	7012306	10 Feb 2011	N/A	-
Vessel Disposal	7013285	21 July 2011	N/A	-
Registration as Chemical Waste Producer	5213-151-C3654-01	24 Mar 2011	N/A	-

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

3.1.6. Summary of the current status on licences and/or permits on environmental protection pertinent and submission for contract no. HK/2012/08 under FEP-08/356/2009 are shown in *Table 3.9* and *Table 3.10*.

## Table 3.9 Cumulative Summary of Valid Licences and Permits under Contract no.HK/2012/08

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental	FEP-06/356/2009	5 Mar 2013	N/A	Valid
Permit	FEP-08/356/2009	1 Aug 2016	N/A	Valid
Notification of Works Under APCO	355439	4 Feb 2013	N/A	Valid
Registration as a Chemical Waste Producer	5213-134-C3790-01	30 Jun 2016	N/A	Valid
Billing Account under Waste Disposal Ordinance	7016883	18 Feb 2013	N/A	Valid
Water Discharge Licence	WT00020594-2014	22 Dec 2014	31 Jan 2019	Valid



Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
	GW-RS0732-18	17 Aug 2018	26 Aug 2018 to 25 Feb 2019	Valid
Construction Noise Permit	GW-RS0597-18	10 Jul 2018	13 Jul 2018 to 12 Jan 2019	Expired
	GW-RS1243-18	31 Dec 2018	13 Jan 2019 to 12 Jul 2019	Valid
	GW-RS0600-18	10 Jul 2018	12 Jul 2018 to 11 Jan 2019	Expired
	GW-RS0913-18	4 Oct 2018	5 Oct 2018 to 4 Apr 2019	Valid

## Table 3.10Summary of submission status under EP-356/2009 and FEP-06/356/2009Condition

FEP Condition	Submission	Date of Submission
Condition 2.8	Silt Curtain Deployment Plan (Rev. 3)	Submitted on 25 Nov 2013 was returned to CSLJV by EPD.
Condition 2.9	Silt Screen Deployment Plan (Rev. 3)	Generally in order as commented by EPD on 19 Sep 2013
Condition 2.23	Noise Management Plan (Rev. 2)	Generally in order as commented by EPD on 15 Aug 2013
Condition 2.24	Landscape Plan (Rev. 3)	Generally in order as commented by EPD on 31 Oct 2013



Contract no. HY/2010/08 – Central - Wan Chai Bypass (CWB) – Tunnel (Slip Road 8)

3.1.7. Summary of the current status on licences and/or permits on environmental protection pertinent and submission for contract no. HY/2010/08 under FEP-07/356/2009 are shown in Table 3.11 and Table 3.12.

Table 3.11	Cumulative Summary of Valid Licences and Permits under Contract no.
HY/2010/08	

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental	FEP-07/356/2009	26 Jul 2013	NA	Valid
Permit	FEP-10/364/2009/B	26 Jul 2013	NA	Valid
Notification of Works Under APCO	357176	2 Apr 2013	N/A	Valid
Registration as a Chemical Waste Producer	WPN5213-147-C1169-44	27 Mar 2013	N/A	Valid
Billing Account under Waste Disposal Ordinance	7017170	27 Mar 2013	N/A	Valid
Billing Account under Waste Disposal Ordinance (Dumping by Vessel)	7020947	22 Dec 2014	N/A	Valid.
Water Discharge	WT00031281-2018	31 Jul 2018	31 Jul 2018 to 31 Jul 2023	Valid
Licence	WT00028744-2017	4 Aug 2017	4 Aug 2017 to 31 Aug 2019	Surrendered
Construction Noise Permit	GW-RS0812-18	7 Sep 2018	12 Sep 2018 to 10 Mar 2019	Valid



Table 3.12	Summary of submission status under EP-356/2009 and FEP-07/356/2009
Condition	

FEP Condition	Submission	Date of Submission
Condition 2.8	Silt Curtain Deployment Plan (Rev 3)	24 Dec 2014
Condition 2.9	Silt Screen Deployment Plan (Rev 3)	21 Nov 2017
Condition 2.23	Noise Management Plan (Rev 2)	25 Mar 2014
Condition 2.24	Landscape Plant (Rev 2)	23 Sep 2014



### 4 Monitoring Requirements

#### 4.1 Noise Monitoring

#### NOISE MONITORING STATIONS

4.1.1. The noise monitoring stations for the Project are listed and shown in *Table 4.1* and *Figure 4.1*. *Appendix 4.1* shows the established Action/Limit Levels for the monitoring works.

Station	Description	
M1a	Footbridge for Ex-Harbour Road Sports Centre*	
M2b	Noon Gun Area	
МЗа	Tung Lo Wan Fire Station	
M4b	Victoria Centre	
M5b	City Garden	
M6	HK Baptist Church Henrietta Secondary School	

Table 4.1 Noise Monitoring Station

Remarks\*: With respect to the demolition of Ex-Harbour Road Sports Centre, the respective noise monitoring station M1a – Harbour Road Sports Centre were finely adjusted on 16 and 25 May 2017 and thereafter to the Footbridge for Harbour Road Sports for noise monitoring

#### NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.1.2. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (Leq). Leq (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods, Leq (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. Supplementary information for data auditing, statistical results such as L10 and L90 shall also be obtained for reference.
- 4.1.3. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
  - One set of measurements between 0700 and 1900 hours on normal weekdays.
- 4.1.4. If construction works are extended to include works during the hours of 1900 0700 as well as public holidays and Sundays, additional weekly impact monitoring shall be carried out during



respective restricted hours periods. Applicable permits under NCO shall be obtained by the Contractor.

### MONITORING EQUIPMENT

- 4.1.5. As referred to in the Technical Memorandum <sup>™</sup> issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.
- 4.1.6. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

## 4.2 Air Monitoring

## AIR QUALITY MONITORING STATIONS

4.2.1. The air monitoring stations for the Project are listed and shown in *Table 4.2* and *Figure 4.1*. *Appendix 4.1* shows the established Action/Limit Levels for the monitoring works.

Table 4.2 Air Monitorir	ng Station
-------------------------	------------

Station ID	Monitoring Location	Description
CMA1b	Harbour Grand Hotel Boundary Wall**	North Point
CMA2a	Causeway Bay Community Centre	Causeway Bay
СМАЗа	CWB PRE Site Office *	Causeway Bay
CMA4a	Society for the Prevention of Cruelty to Animals	Wan Chai
CMA5b	Pedestrian Plaza***	Wan Chai
CMA6a	WDII PRE Site Office *	Wan Chai

Remarks\*: As per the ENPC meeting in March 2011, the monitoring stations CMA3a – Future CWB site office at Wanchai Waterfront Promenade was renamed as remark.

Remarks\*\*: The location ID of monitoring station CMA1b was updated as "Harbour Grand Hotel Boundary Wall" from 05 June 2017 onwards.



Remarks\*\*\*: The station ID and monitoring location was updated in December 2014 with respect to monitoring station relocation.

### AIR MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 4.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.
- 4.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.

#### SAMPLING PROCEDURE AND MONITORING EQUIPMENT

- 4.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:
  - 0.6 1.7 m3 per minute adjustable flow range;
  - equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
  - installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
  - capable of providing a minimum exposed area of 406 cm2;
  - flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
  - equipped with a shelter to protect the filter and sampler;
  - incorporated with an electronic mass flow rate controller or other equivalent devices;
  - equipped with a flow recorder for continuous monitoring;
  - provided with a peaked roof inlet;
  - incorporated with a manometer;
  - able to hold and seal the filter paper to the sampler housing at horizontal position;
  - easily changeable filter; and
  - capable of operating continuously for a 24-hour period.
- 4.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC



shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

#### LABORATORY MEASUREMENT / ANALYSIS

- 4.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.
- 4.2.8. An alternative non-HOKLAS accredited laboratory was set-up for carrying out the laboratory analysis, the laboratory equipment was approved by the ER on 8 February 2011 and the measurement procedures were witnessed by the IEC. Any measurement performed by the laboratory was be demonstrated to the satisfaction of the ER and IEC. IEC shall regularly audit to the measurement performed by the laboratory to ensure the accuracy of measurement results.
- 4.2.9. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.
- 4.2.10. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.
- 4.2.11. All the collected samples shall be kept in a good condition for 6 months before disposal.

### IMPACT MONITORING FOR ODOUR PATROL

- 4.2.12. Odour patrols along the shorelines of Causeway Bay Typhoon Shelter and ex-Wan Chai Public Cargo Working Area when there is temporary reclamation in Causeway Bay Typhoon Shelter and/or in the ex-Wan Chai Public Cargo Working Area, or when there is dredging of the odorous sediment and slime at the south-western corner of the Causeway Bay Typhoon Shelter. Odour patrols will be carried out at bi-weekly intervals during July, August and September by a qualified person of the ET who shall:
  - be at least 16 years of age;
  - be free from any respiratory illnesses; and
  - not be allowed to smoke, eat, drink (except water) or use chewing gum or sweets 30 min
  - before and during odour patrol



- 4.2.13. Odour patrol shall be conducted by independent trained personnel / competent persons patrolling and sniffing around the shore as shown in *Figure 4.1* to detect any odour at the concerned hours (afternoon is preferred for higher daily temperature).
- 4.2.14. The qualified person will use the nose (olfactory sensor) to sniff odours at different locations. The main odour emission sources and the areas to be affected by the odour nuisance will be identified.
- 4.2.15. The perceived odour intensity is to be divided into 5 levels which are ranked in the descending order as follows:
  - 0 Not detected. No odour perceived or an odour so weak that it cannot be easily characterized or described;
  - 1 Slight Identifiable odour, and slight chance to have odour nuisance;
  - 2 Moderate Identifiable odour, and moderate chance to have odour nuisance;
  - 3 Strong Identifiable, likely to have odour nuisance;
  - 4 Extreme Severe odour, and unacceptable odour level.
- 4.2.16. The findings including odour intensity, odour nature and possible odour sources, and also the local wind speed and direction at each location will be recorded. In addition, some relevant meteorological and tidal data such as daily average temperature, and daily average humidity, on that surveyed day will be obtained from the Hong Kong Observatory Station for reference. The Action and Limit levels for odour patrol are shown in <u>Appendix 4.1.</u>
- 4.2.17. The qualified odour patrol member has individual n-butanol thresholds complied with the requirement of European Standard Method of Air Quality Determination of Odour Concentration by Dynamic Olfactometry (EN13725) in the range of 20 to 80 ppb.

# 4.3 Water Quality Monitoring

- 4.3.1. The EIA Report has identified that the key water quality impact would be associated with the dredging works during the construction phase. Marine water quality monitoring for dissolved oxygen (DO), suspended solid (SS) and turbidity is therefore recommended to be carried out at selected WSD flushing water intakes. The impact monitoring should be carried out during the proposed dredging works to ensure the compliance with the water quality standards.
- 4.3.2. The updated EM&A Manual for EP-356/2009 (Version in March 2011) is approval by EPD on 29 April 2011. As such, the Action Level and Limit Level for the wet season (April September) will be effected and applied to the water quality monitoring data from 30 April 2011.

#### Water Quality Monitoring Stations

4.3.3. Water quality monitoring was undertaken at 8 monitoring stations for WSD salt water intakes and cooling water intakes along the seafront of the Victoria Harbour in the reporting month.



The proposed water quality monitoring stations of the Project are shown in *Table 4.3* and *Figure 4.1*. *Appendix 4.1* shows the established Action/Limit Levels for the monitoring works.

Station Ref.	Location	Easting	Northing
WSD Salt Water	Intake		1
WSD19	Sheung Wan	833415.0	816771.0
Cooling Water I	ntake		
C1	HKCEC Extension	835885.6	816223.0
C7	Windsor House	837193.7	816150.0
P1	HKCEC Phase I	835774.7	816179.4
P3	The Academy of performing Arts	835824.6	816212.0
P4	Shui on Centre	835865.6	816220.0
P5	Government Buildings	835895.2	816215.2
	(Wanchai Tower / Revenue		
	Tower / Immigration Tower)		
Cooling Water I	ntake / WSD Salt Water Intake	,	
RW21-P789	Great Eagle Centre/ Sun Hung Kai	836268.0	816020.0
	Centre/ WSD Wanchai salt water		
	intake / China Resources Building		

Remarks: - The cessation of seawater intake operation for C6 was confirmed on 17 May 2011 and the water quality monitoring at C6 was then terminated since 17 May 2011.

- 4-week post construction water quality monitoring at WSD9, WSD10, WSD15 and WSD17 were completed on 6 Feb 2012 and the water quality monitoring at WSD 10 and WSD15 were temporary suspended since 8 Feb 2012, and WSD9 and WSD17 was implemented with respect to HK/2009/02 from 8 Feb 2012 onwards.
- C8 and C9 were implemented with respect to HY/2009/19 from 28 Jan 2012.
- C8 & C9 were temporary suspended since 4 March 2013.
- WSD7 and WSD20 water quality monitoring were temporarily suspended from 27 Apr 2012.
- C2, C3 C4e and C4w water quality monitoring station was temporarily suspended since
   22 Apr 2013
- P1, P3, P4 and P5 were commenced since 24 Apr 2013
- C5e and C5w water quality monitoring station was temporarily suspended since 29 Jul 2013.
- WSD21 water quality monitoring station was temporarily suspended since 12 Mar 2014
- WSD9 and WSD17 water quality monitoring station was temporarily suspended since 8 Sep 2014 flood tide.



- The water quality monitoring station C1 shall be associated with Contract No. HK/2009/02 upon commencement of marine works under DP3 at WCR3 area.
- The water quality monitoring station RW21-P789 was adjusted to RW21-P789E and RW21-P789W since 28 November 2016 ebb-tide.
- The water quality monitoring was reverted to previous monitoring station RW21-P789 from PW21-P789E and RW21-P789W from 25 January 2017 onwards.

### WATER QUALITY PARAMETERS

- 4.3.4. Monitoring of dissolved oxygen (DO), turbidity and suspended solids (SS) shall be carried out at WSD flushing water intakes and cooling water intakes. DO and Turbidity are measured in-situ while SS is determined in laboratory.
- 4.3.5. In association with the water quality parameters, other relevant data shall also be measured, such as monitoring location/position, time, sampling depth, water temperature, pH, salinity, dissolved oxygen (DO) saturation, weather conditions, sea conditions, tidal stage, and any special phenomena and work underway at the construction site etc.

## SAMPLING PROCEDURES AND MONITORING EQUIPMENT

4.3.6. The interval between two sets of monitoring should not be less than 36 hours except where there are exceedances of Action and/or Limit Levels, in which case the monitoring frequency will be increased. *Table 4.4* shows the proposed monitoring frequency and water quality parameters. Duplicate in-situ measurements and water sampling should be carried out in each sampling event. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.

Activities	Monitoring Frequency <sup>1</sup>	Parameters <sup>2</sup>
During the 4-week baseline monitoring period	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
During marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
After completion of marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity

Table 4.4 Marine Water	r Quality Monitoring	Frequency and Parameters
------------------------	----------------------	--------------------------

Notes:

- 1. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.
- 2. Turbidity should be measured in situ whereas SS should be determined by laboratory.



## DISSOLVED OXYGEN AND TEMPERATURE MEASURING EQUIPMENT

- 4.3.7. The instrument should be a portable, weatherproof dissolved oxygen measuring instrument complete with cable, sensor, comprehensive operation manuals, and use a DC power source. It should be capable of measuring:
  - a dissolved oxygen level in the range of 0-20 mg/l and 0-200% saturation
  - a temperature of 0-45 degree Celsius
- 4.3.8. It should have a membrane electrode with automatic temperature compensation complete with a cable. Sufficient stocks of spare electrodes and cables should be available for replacement where necessary. (e.g. YSI model 59 meter, YSI 5739 probe, YSI 5795A submersible stirrer with reel and cable or an approved similar instrument).
- 4.3.9. Should salinity compensation not be build-in in the DO equipment, in-situ salinity shall be measured to calibrate the DO equipment prior to each DO measurement.

#### TURBIDITY MEASUREMENT INSTRUMENT

4.3.10. The instrument should be a portable, weatherproof turbidity-measuring instrument complete with comprehensive operation manual. The equipment should use a DC power source. It should have a photoelectric sensor capable of measuring turbidity between 0-1000 NTU and be complete with a cable (e.g. Hach model 2100P or an approved similar instrument).

#### SAMPLER

4.3.11. A water sampler comprises a transparent PVC cylinder, with a capacity of not less than 2 litres, and can be effectively sealed with latex cups at both ends. The sampler should have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth (e.g. Kahlsico Water Sampler or an approved similar instrument).

# SAMPLE CONTAINER AND STORAGE

4.3.12. Water samples for suspended solids measurement should be collected in high-density polythene bottles, packed in ice (cooled to 4°C without being frozen), and delivered to ALS Technichem (HK) Pty Ltd. as soon as possible after collection for analysis.

#### WATER DEPTH DETECTOR

4.3.13. A portable, battery-operated echo sounder shall be used for the determination of water depth at each designated monitoring station. This unit can either be handheld or affixed to the bottom of the workboat, if the same vessel is to be used throughout the monitoring programme.

#### <u>SALINITY</u>

4.3.14. A portable salinometer capable of measuring salinity in the range of 0-40 ppt shall be provided for measuring salinity of the water at each of monitoring location.



## MONITORING POSITION EQUIPMENT

4.3.15. A hand-held or boat-fixed type digital Global Positioning System (GPS) with waypoint bearing indication or other equivalent instrument of similar accuracy shall be provided and used during monitoring to ensure the monitoring vessel is at the correct location before taking measurements.

### CALIBRATION OF IN-SITU INSTRUMENTS

- 4.3.16. All in-situ monitoring instrument shall be checked, calibrated and certified by a laboratory accredited under HOKLAS or equivalent before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the water quality monitoring. Responses of sensors and electrodes should be checked with certified standard solutions before each use. Wet bulb calibration for a DO meter shall be carried out before measurement at each monitoring location.
- 4.3.17. For the on site calibration of field equipment by the ET, the BS 127:1993, "Guide to Field and on-site test methods for the analysis of waters" should be observed.
- 4.3.18. Sufficient stocks of spare parts should be maintained for replacements when necessary. Backup monitoring equipment shall also be made available so that monitoring can proceed uninterrupted even when some equipment is under maintenance, calibration, etc.
- 4.3.19. Current calibration certificates of equipments are presented in <u>Appendix 4.2.</u>

#### LABORATORY MEASUREMENT / ANALYSIS

4.3.20. Analysis of suspended solids has been carried out in a HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd. Water samples of about 1L shall be collected at the monitoring stations for carrying out the laboratory SS determination. The SS determination work shall start within 24 hours after collection of the water samples. The SS determination shall follow APHA 19ed or equivalent methods subject to the approval of IEC and EPD.

# ENHANCED WATER QUALITY MONITORING IN THE EX-WAN CHAI PUBLIC CARGO WORKING AREA AND THE CAUSEWAY BAY TYPHOON SHELTER

- 4.3.21. The enhanced water quality monitoring and audit programme is to avoid aggravation of odour nuisance from seawater arising from temporary reclamation in the ex-Wan Chai Public Cargo Working Area and the Causeway Bay Typhoon Shelter.
- 4.3.22. Dissolved oxygen monitoring at the intakes C6 and C7 in Causeway Bay Typhoon Shelter when there is temporary reclamation in Causeway Bay Typhoon Shelter and at the south-western and south-eastern corners of the ex-Wan Chai Public Cargo Working Area. The proposed water quality monitoring stations of the Project are shown in *Table 4.5* and *Figure* <u>4.1.</u>



Table 4.5	Marine Water Quality Stations for Enhanced Water Quality Monitoring
-----------	---

Station	Location
C6	Excelsior Hotel
C7	Windsor House
Ex-WPCWA-SW	South-western of the ex-Wan Chai Public Cargo Working Area
Ex-WPCWA-SE	South-eastern of the ex-Wan Chai Public Cargo Working Area

Remarks:

- Enhanced DO monitoring at Windsor House Cooling (Station Ref: C7) was temporarily suspended since 22 October 2014 with respect to the formation of temporary reclamation zone TS3 and was resumed from 1 February 2018 onwards with respect to the completion of removal of temporary reclamation zone.
- Enhanced DO monitoring at Monitoring station Ex-WPCWA SE was temporarily suspended from 31 August 2015 with respect to seawall reinstatement works and formation of active works area. The Enhance DO monitoring at Ex-WPCWA SE was resumed on 11 May 2016 due to completed section of seawall reinstatement works at Ex-PCWA.
- 4.3.23. The monitoring of dissolved oxygen are to be carried out 3 days per week, at mid-flood and mid-ebb tides for 3 water depths (1m below water surface, mid-depth and 1m above sea bed, except where the water depth less than 6m, the mid-depth may be omitted. If the water depth be equal to or less than 3m, only the mid-depth will be monitored).

#### DAILY SS MONITORING AND 24 HOURS TURBIDITY MONITORING SYSTEM

- 4.3.24. During dredging of the sediment at the south-western corner of the Causeway Bay Typhoon Shelter, daily monitoring of suspended solids and 24 hour monitoring of turbidity at the cooling water intakes (C6 and C7) shall be conducted.
- 4.3.25. The 24 hours monitoring of turbidty at the cooling water intakes (C6 and C7) shall be established by setting up a continuous water quality monitoring station in front of the intakes during the dredging activities. The monitoring system include the turbidity sensor and data logger which is capable of data capturing at every 5 minutes. The data sahll be downloaded daily and compared with the Action and Limit level determined during the baseline water quality monitoring at the cooling water intake locations.

# ADDITIONAL DISSOVLED OXYGEN MONITORING FOR CULVERT L WATER DISCHARGE FLOW

4.3.26. In response to the Condition 2.18 of the Environmental Permit no. EP-356/2009 requiring that a silt curtain / impermeable barrier system be installed to channel water discharge flow from Culvert L to locations outside the embayment area, a proposed replacement of the



requirement with additional dissolved oxygen monitoring has been conducted at three monitoring stations, namely A, B and C between the eastern seawall of Central Reclamation Phase III and the HKCEC Extension since November 2011 under EP-356/2009 so that DO level between the eastern seawall of Central Reclamation Phase II and the HKCEC extension could be continuously monitored.

- 4.3.27. With respect to the commencement of dredging works under HK/2012/08 and the installation of MTR precast protection unit, the enhanced water quality monitoring for Culvert L was temporarily suspended since 24 July 2013
- 4.3.28. The monitoring of dissolved oxygen are to be carried out once per week, at mid-flood and mid-ebb tides for 3 water depths (1m below water surface, mid-depth and 1m above sea bed, except where the water depth less than 6m, the mid-depth may be omitted. If the water depth be equal to or less than 3m, only the mid-depth will be monitored).



# 5. Monitoring Results

- 5.0.1. The environmental monitoring will be implemented based on the division of works areas of each designed project managed under different contracts with separate FEP applied by individual contractors. Overall layout showing work areas of various contracts, latest status of work commencement and monitoring stations is shown in <u>Figure 2.1</u> and <u>Figure 4.1</u>. The monitoring results are presented in according to the Individual Contract(s).
- 5.0.2. In the reporting month, the concurrent contracts are as follows:
  - Contract no. HK/2009/02 Wan Chai Development Phase II Central-Wan Chai Bypass at Wan Chai East
  - Contract no. HY/2009/19- Central- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link
  - Contract no. HK/2012/08 Wan Chai Development Phase II Central- Wan Chai Bypass at Wan Chai West
- 5.0.3. As confirmed by WDII RSS, the marine construction works under Contract HK/2009/01 have been completed since 24 July 2017, the monitoring association with Contract HK/2009/01 and relevant reporting has been ceased in the reporting month.
- 5.0.4. As confirmed by CWB RSS, the marine construction works under Contract HY/2009/15 and relevant reporting have been completed by 19 June 2017, the monitoring association with Contract HY/2009/15 and relevant reporting has been ceased in the reporting month.
- 5.0.5. As confirmed by CWB RSS, the marine construction works under Contract HY/2010/08 and relevant reporting have been completed by 21 September 2018, the air monitoring stations namely CMA3a CWB PRE Site Office and noise monitoring station namely M2b Noon day gun area and M3a Tung Lo Wan Fire Station association with Contract HY/2010/08 and relevant reporting has been ceased in the reporting month.
- 5.0.6. The environment monitoring schedules for reporting month and coming month are presented in *Appendix 5.1*.



# 5.1 Noise Monitoring Results

<u>Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass</u> <u>at WanChai East</u>

5.1.1. The proposed division of noise monitoring stations are summarized in *Table 5.1* below.

Table 5.1 Noise Monitoring Station for Contract nos. HK/2009/02

Station	Description
M1a	Footbridge for Ex-Harbour Road Sports Centre

- 5.1.2. No action or limit level exceedances was recorded in the reporting period.
- 5.1.3. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in <u>Appendix</u> <u>5.2.</u>

Contract no. HY/2009/19- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

5.1.4. The proposed division of noise monitoring stations are summarized in *Table 5.3* below.

Station	Description
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School

 Table 5.3
 Noise Monitoring Station for Contract no. HY/2009/19

- 5.1.5. Two limit level exceedance was recorded at M6 Hong Kong Baptist Church Henrietta Secondary School on 18 and 25 January 2019 in the reporting period.
- 5.1.6. No construction works was conducted on 18 January 2019 under HY/2009/19 around the monitoring location and nearby traffic noise was observed as major noise source during monitoring. As such, the exceedance was considered as non-Project related.
- 5.1.7. No construction works was conducted on 25 January 2019 under HY/2009/19 around the monitoring location and nearby traffic noise was observed as major noise source during monitoring. As such, the exceedance was considered as non-Project related.
- 5.1.8. Noise monitoring results measured in this reporting period are reviewed and summarized.
   Details of noise monitoring results and graphical presentation can be referred in <u>Appendix</u>
   <u>5.2.</u>



# 5.2 Air Monitoring Results

Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

5.2.1 Air monitoring was commenced in mid-January 2011 for the land-filling work for Contract no. HK/2009/02. The proposed division of air monitoring stations are summarized in *Table 5.6* below.

Station	Description
CMA3a	CWB PRE Site Office
CMA4a	Society for the Prevention of Cruelty to Animals

 Table 5.6
 Air Monitoring Station for Contract no. HK/2009/02

- 5.2.2 No action or limit level exceedance was recorded in the reporting period.
- 5.2.3 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in *Appendix 5.3*.

Contract no. HY/2009/19- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

5.2.4 The proposed division of air monitoring stations are summarized in *Table 5.8* below.

Table 5.8 Air Monitoring Stations for Contract no. HY/2009/19

Station	Description
CMA1b	Harbour Grand Hotel Boundary Wall
CMA2a	Causeway Bay Community Centre

- 5.2.5 No action or limit level exceedance was recorded in the reporting period.
- 5.2.6 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in *Appendix 5.3*.



<u>Contract no. HK/2012/08- Wan Chai Development Phase II – Central-Wan Chai Bypass at</u> Wan Chai West

5.2.7 The proposed division of air monitoring stations are summarized in *Table 5.9* below.

 Table 5.9
 Air Monitoring Stations for Contract no. HK/2012/08

Station	Description
CMA5b	Pedestrian Plaza
CMA6a	WDII PRE Site Office

- 5.2.8 No action or limit level exceedance was recorded in the reporting period.
- 5.2.9 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in *Appendix 5.3*.

## 5.3 Water quality monitoring Results

- 5.3.1 Action and Limit level of water quality monitoring was transited from wet season to dry season from 01 October 2018.
- 5.3.2 Water quality monitoring station C7 and Enhance DO monitoring station C6 shall be associated with Contract HY/2010/08, upon confirmation of marine construction works completion under Contract HY/2009/15 at CBTS area and Ex-PCWA area since 19 June 2017.
- 5.3.3 Referring to CWB RSS confirmation on the completion of marine construction activities within the Ex-PCWA area and the completion of the post construction water quality monitoring, the respective Enhance DO Monitoring within Ex-PCWA for monitoring station Ex-PCWA SE and Ex-PCWA SW was temporarily suspended since 07 March 2017 ebb tide onwards.
- 5.3.4 With respect to the reinstatement of the silt screen system for Cooling Water Intakes P7, P8, P9 and WSD Water Intake RW21, the respective water quality monitoring was reverted to the previous monitoring location for Water Quality Monitoring Station RW21-P789 from water quality stations RW21-P789 East (RW21-P789E) and RW21-P789 West (RW21-P789W) from 25 January 2017 onwards.
- 5.3.5 With respect to the temporarily suspension of marine construction works at WCR3 Area by Contract HK/2009/02, the installed silt screen for intake group (P7, P8, P9 and WSD21) was removed on 26 November 2016.
- 5.3.6 As advised by the Contractor of HK/2009/01, all silt screen remains removal works at P1, P3, P4, P5 and C1 water quality monitoring stations were completed on 8 May 2016.



- 5.3.7 With respect to the marine works undertaken at WCR3 by Contract HK/2009/02, the respective water quality monitoring station C1 associated with Contract HK/2009/01 was updated as in association with Contract HK/2009/01 and Contract HK/2009/02.
- 5.3.8 With respect to the marine works undertaken at CBTS by Contract HY/2010/08, the respective water quality monitoring station C7 associated with Contract HY/2009/15 was updated as in association with Contract HY/2009/15 and Contract HY/2010/08.
- 5.3.9 With respect to the marine works undertaken at HKCEC2 by Contract HK/2012/08, the respective water quality monitoring station WSD19, P1, P3, P4, and P5 were associated with Contract HK/2012/08.
- 5.3.10 As confirmed by WDII RSS, the marine construction works under Contract HK/2009/01 have been completed since 24 July 2017, the monitoring association with Contract HK/2009/01 and relevant reporting has been ceased in the reporting month.
- 5.3.11 As confirmed by CWB RSS, the marine construction works under Contract HY/2009/15 and relevant reporting have been completed by 19 June 2017, the monitoring association with Contract HY/2009/15 and relevant reporting has been ceased in the reporting month.
- 5.3.12 Referring to CWB RSS confirmation on the completion of marine works within the TS3 area and the completion of the post construction water quality monitoring, the respective water quality monitoring within TS3 for monitoring station C7 was temporarily suspended since 29 October 2018 onwards.
- 5.3.13 Referring to WDII RSS confirmation on the completion of marine works under HK/2012/08 within the EP-356 area on 2 January 2019, the four weeks post-construction monitoring for respective water quality monitoring stations P1, P3, P4, P5 and WSD19 within EP-356 area was started on 2 January 2019.



Table 5.11 Water quality Monitoring Stations for contracts with respect to remaining
DP3 work areas after the completion of DP5 & DP6 in 2012 and intake diversion in 2013

Contract No.	Remaining DP3 and work area(s)	Relevant Water quality monitoring Stations,	Division of WQM w.r.t tentative works commenced / to be commenced
HK/2009/02	WCR3, WCR4, TWCR4	RW21-P789 <sup>2</sup> , C1 <sup>1</sup>	Apr 2013
HK/2012/08	HKCEC2W, HKCEC2E	WSD19, P1 <sup>3</sup> , P3 <sup>3</sup> , P4 <sup>3</sup> , P5 <sup>3</sup>	Aug 2013
HY/2010/08	TCBR3, TCBR4	C6 <sup>4</sup> , C7 <sup>4</sup> (plus enhanced DO monitoring)	Mar 2014

Remarks:

- 1. The water quality monitoring station C1 shall be associated with Contract No. HK/2009/02 upon commencement of marine works under DP3 at WCR3 area.
- 4 intakes (re-provisioned Wanchai WSD intake, Great Eagle Centre, China Resources Centre & Sun Hung Kai Centre constructed adjacent to each other) taken as a single group for silt screen protection and monitoring. Re-provisioned intake reference: P1: HKCEC Phase 1; P3: APA, P4: Shui On; P5: Government Buildings (Wanchai Tower / Revenue Tower / Immigration Tower)
- 3. The water quality monitoring stations for WSD19, P1, P3, P4, P5 shall be associated with Contract No. HK/2009/01 prior to their transition to Contract HK/2012/08.
- Enhance DO monitoring station C6 and water quality monitoring station C7 shall be associated with Contract HY/2010/08, upon confirmation of marine construction works completion under Contract HY/2009/15 at CBTS area and Ex-PCWA area since 19 June 2017.
- Referring to CWB RSS confirmation on the completion of marine construction activities within the TS3 area and the completion of the post construction water quality monitoring, the respective Enhance DO Monitoring within TS3 for monitoring station C6 and C7 was temporarily suspended since 05 March 2018 onwards.
- 6. With respect to WDII RSS confirmation on the completion of marine works under Contract HK/2009/01 since 24 July 2017, the association of WQM station C1 under Contract HK/2009/01 has been ceased in the November 2017 reporting month.
- Referring to CWB RSS confirmation on the completion of marine works within the TS3 area and the completion of the post construction water quality monitoring, the respective water quality monitoring within TS3 for monitoring station C7 was temporarily suspended since 29 October 2018 onwards
- Referring to WDII RSS confirmation on the completion of marine works under HK/2012/08 within the EP-356 area on 2 January 2019, the four weeks post-construction monitoring for respective water quality monitoring stations P1, P3, P4, P5 and WSD19 within EP-356 area was started on 2 January 2019.



<u>Contract no. HK/2009/02 - Wan Chai Development Wan Chai Development Phase II –</u> <u>Central – Wan Chai Bypass at WanChai East</u>

5.3.14 Water quality monitoring for Contract no. HK/2009/02 was commenced on 8 July 2010. The proposed division of water quality monitoring stations are summarized in *Table 5.13* below.

Table 5.13 Water quality Monitoring Stations for Contract no. HK/2009/02

Station Ref.	Location	Easting	Northing		
Cooling Water Intake					
C1	HKCEC Extension	835885.6	816223.0		
Cooling Water Int	Cooling Water Intake / WSD Salt Water Intake				
RW21-P789	Great Eagle Centre/ Sun Hung Kai Centre/ WSD Wanchai salt water intake / China Resources Building	836268.0	816020.0		

- 5.3.15 No action level exceedance was recorded in the reporting period.
- 5.3.16 Water quality monitoring results measured in this reporting period are reviewed and summarized. Details of water quality monitoring results and graphical presentation can be referred in *Appendix 5.4.*



Contract no. HK/2012/08 - Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

5.3.17 Water quality monitoring for Contract no. HK/2012/08 was commenced on 5 March 2013. The proposed division of water quality monitoring stations are summarized in *Table 5.14* below.

Table 5.14 Water quality Monitoring Stations for Contract no. HK/2012/08

Station Ref.	Location	Easting	Northing			
WSD Salt Wat	WSD Salt Water Intake					
WSD19	Sheung Wan	833415.0	816771.0			
Cooling Wate	Cooling Water Intake					
P1	HKCEC Phase I	835774.7	816179.4			
P3	The Academy of performing Arts	835824.6	816212.0			
P4	Shui on Centre	835865.6	816220.0			
P5	Government Buildings (Wanchai Tower / Revenue Tower / Immigration Tower)	835895.2	816215.2			

5.3.18 One action level exceedance of suspended solids was recorded on 25 January 2019 at P5 in the reporting period.

- 5.3.19 No marine construction activity was conducted under Contract HK/2012/08 on the monitoring date while the location of the construction area was at downstream of monitoring station P5 during monitoring period. In view of the above, it is considered that the exceedance was not related to Project works.
- 5.3.20 Water quality monitoring results measured in this reporting period are reviewed and summarized. Details of water quality monitoring results and graphical presentation can be referred in *Appendix 5.4.*



# 5.4 Waste Monitoring Results

<u>Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East</u>

5.3.21 Details of the waste disposal in the reporting period are summarized in *Table 5.18*.

Table 5.18	Details of Waste Disposal for Contract no. HK/2009/02
10010 0.10	

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m <sup>3</sup>	2619.1	312333.2	TKO137 / TM 38
Inert C&D materials recycled, m <sup>3</sup>	NIL	18161	N/A
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	1515.103	SENT Landfill
Non-inert C&D materials recycled, m <sup>3</sup>	N/A	N/A	N/A
Chemical waste disposed, kg	NIL	13860	SENT Landfill
Marine Sediment (Type 1 – Open Sea Disposal), m <sup>3</sup>	NIL	240222 (Bulk volume)	South of Cheung Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m <sup>3</sup>	NIL	146445 (Bulk volume)	East of Sha Chau



<u>Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon</u> <u>Shelter Section)</u>

5.3.22 Details of the waste disposal in the reporting period are summarized in Table 5.19

 Table 5.19
 Details of Waste Disposal for Contract no. HY/2009/15

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds	Remarks
Inert C&D materials	NIL	141579.2	Tuen Mun Area 38	NIL
disposed, m <sup>3</sup>	NIL	65216	TKO137 FB	NIL
Inert C&D materials	NIL	8127.21	HY/2010/08	NIL
recycled, m <sup>3</sup>	NIL	304	Ex-PCWA	NIL
	NIL	111.9	TS4	NIL
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	252.2	SENT Landfill	NIL
Non-inert C&D materials recycled, kg	NIL	299361.5	N/A	NIL
Chemical waste disposed, kg	NIL	8,200	N/A	NIL
Marine Sediment (Type 1 – Open Sea Disposal), m <sup>3</sup>	NIL (Bulk Volume)	156909 (Bulk Volume)	Cheung Chau South	Dredging from TCBR1E / TCBR1W / TCBR2/ TCBR3 / TCBR4 / Maintenance dredging
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m <sup>3</sup>	NIL (Bulk Volume)	327746 (Bulk Volume)	East of Sha Chau / South of the Brothers	Dredging from TCBR1E / TCBR1W / TCBR2/ TCBR3 / TCBR4 / Maintenance dredging
Marine Sediment (Type 3 – Special Treatment / Disposal contained in Geosynthetic Containers) m <sup>3</sup>	NIL (Bulk Volume)	12640 (Bulk Volume)	East of Sha Chau / South of the Brothers	Dredging from TCBR1W / Maintenance dredging
Marine Sediment (Type 2 – Confined Marine Disposal), m <sup>3</sup>	NIL	9350 (Bulk Volume)	East of Sha Chau	Dredging from Eastern Breakwater of CBTS



Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds	Remarks
Marine Sediment (Type 1 – Open Sea Disposal) , m3	NIL (Bulk Volume)	600 (Bulk Volume)	East Sha Chau / South of The Brothers	Dredging from Phase 3 Mooring Re-arrangement
Marine Sediment (Type 2– Confined Marine Disposal) , m3	NIL (Bulk Volume)	14,780 (Bulk Volume)	South of The Brothers	Dredging from Phase 3 Mooring Re-arrangement
Marine Sediment (Type 3 – Special Treatment / Disposal contained in Geosynehetic Containers) , m3	NIL (Bulk Volume)	2,760 (Bulk Volume)	South of The Brothers	Dredging from Phase 3 Mooring Re-arrangement



Contract no. HY/2009/19 –Central- WanChai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

5.3.23 Details of the waste disposal in the reporting period are summarized in *Table 5.20*.

## Table 5.20 Details of Waste Disposal for Contract no. HY/2009/19

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m <sup>3</sup>	NIL	355921.04	TM38
Inert C&D materials recycled, m <sup>3</sup>	NIL	59367	N/A
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	1068.6	N/A
Non-inert C&D materials recycled, kg	NIL	333.14	N/A
Chemical waste disposed, L	NIL	2.12	N/A
Marine Sediment (Type 1 – Open Sea Disposal), m <sup>3</sup>	NIL	162	South Cheung Chau
Marine Sediment (Type 2 – Confined Marine Disposal) , m <sup>3</sup>	NIL	681	East Sha Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m3	NIL	4976.00	East Sha Chau



<u>Contract no. HK/2012/08 –Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> <u>Wan Chai West</u>

5.3.24 Details of the waste disposal in the reporting period are summarized in *Table 5.21*.

### Table 5.21 Details of Waste Disposal for Contract no. HK/2012/08

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m <sup>3</sup> *	NIL	4131	TM38
	NIL	273	TKO137
Inert C&D materials recycled, m <sup>3</sup>	NIL	NIL	N/A
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	400	SENT
Non-inert C&D materials recycled, kg	NIL	NIL	N/A
Chemical waste disposed, L	NIL	NIL	N/A
Marine Sediment (Type 1 – Open Sea Disposal), m <sup>3</sup>	NIL (Bulk volume)	31759 (Bulk volume)	South of Cheung Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m3	NIL (Bulk volume)	108542 (Bulk volume)	South of The Brothers (from 27 Aug 2013 onwards)



Contract no. HY/2010/08 – Central - Wan Chai Bypass (CWB) – Tunnel (Slip Road 8)

5.3.25 Details of the waste disposal in the reporting period are summarized in *Table 5.22* 

## Table 5.22 Details of Waste Disposal for Contract no. HY/2010/08

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m <sup>3</sup>	NIL NIL	95094.759 19739.4	TM38 TKO137
Inert C&D materials recycled, m <sup>3</sup>	NIL	NIL	N/A
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	NIL	N/A
Non-inert C&D materials recycled, kg	NIL	NIL	N/A
Chemical waste disposed, L	NIL	NIL	N/A
Marine Sediment (Type 1 – Open Sea Disposal)	NIL	62559.4	South Cheung Chau / Brothers Island *
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine disposal)	NIL	28309.2	Brothers Island
Marine Sediment (Type 3 – Special Treatment)	NIL	7780	Brothers Island



# 6. Compliance Audit

6.0.1. The Event Action Plan for construction noise, air quality and water quality are presented in *Appendix 6.1.* 

# 6.1 Noise Monitoring

Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

6.1.1 No action or limit level exceedance was recorded in the reporting period.

<u>Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island</u> <u>Eastern Corridor Link</u>

6.1.2 Two limit level exceedance was recorded at M6 – Hong Kong Baptist Church Henrietta Secondary School on 18 and 25 January 2019 in the reporting period. After the investigation, the exceedance was concluded as non-project related.

# 6.2 Air Monitoring

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East (CWB Tunnel)</u>

6.2.1 No action or limit level exceedance was recorded in the reporting period.

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

6.2.2 No action or limit level exceedance was recorded in the reporting period.

Contract no. HK/2012/08 Wan Chai Development Phase II - Central-Wan Chai Bypass at Wan Chai West

6.2.3 No action or limit level exceedance was recorded in the reporting period.

# 6.3 Water Quality Monitoring

Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East

6.3.1 No action or limit level exceedance was recorded in the reporting period.

<u>Contract no. HK/2012/08- Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> <u>Wan Chai West</u>

6.3.2 One action level exceedance of suspended solids was recorded on 25 January 2019 at P5 in the reporting period. After the investigation, the exceedance was concluded as non-project related.



## 6.4 Review of the Reasons for and the Implications of Non-compliance

6.4.1 There was no non-compliance from the site audits in the reporting period. The observations and recommendations made in each individual site audit session were presented in Section 8.

#### 6.5 Summary of action taken in the event of and follow-up on non-compliance

6.5.1 There was no particular action taken since no non-compliance was recorded from the site audits in the reporting period.



# 7. Cumulative Construction Impact due to the Concurrent Projects

- 7.0.1. According to Condition 3.4 of the EP-356/2009, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Central Reclamation Phase III, Central-Wanchai Bypass and Island Eastern Corridor Link projects.
- 7.0.2. According to the Final EM&A Report of Central Reclamation Phase III (CRIII) for Contract HK 12/02, the major construction activities were completed by end of January 2014 and no construction activities were undertaken thereafter and the water quality monitoring was completed in October 2011 and no Project-related exceedance was recorded for air and noise monitoring. It can be concluded that cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was insignificant.
- 7.0.3. According to the construction programme of Central-Wanchai Bypass at Wanchai West at the Central Reclamation Phase III area include roadworks, drainage, seawall coping and junction modification were performed in January 2019 reporting period. As no project related exceedance were recorded during the reporting period, cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was considered as insignificant.
- 7.0.4. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activities under Wan Chai Development Phase II were road and drains construction and trimming seabed profile at Wan Chai. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were ventilation building ABWF works and junction modification at Central; road works, drainage improvement work, utility diversion works and landscape works at Victoria Park; bridge noise enclosure installation works, road works, drainage works, soft landscape works and ventilation building ABWF work at North Point area in the reporting period. In addition, other non-Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects were observed undertaken at Wan Chai North and North Point area.
- 7.0.5. No significant air impact from construction activities was anticipated in the reporting month. Besides, no project related exceedance was recorded during the air and noise environmental monitoring events in the reporting month. Thus, it is evaluated that the cumulative construction impact from the concurrent projects including Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) was insignificant.



# 8. Environmental Site Audit

- 8.0.1. During this reporting month, weekly environmental site audits were conducted for Contracts no. HK/2009/02, HY/2009/19, HK/2012/08 and HY/2010/08. No non-conformance was identified during the site audits.
- 8.0.1. Site inspections for Contract no. HK/2009/02 were conducted in the reporting period. The results of these inspections and outcomes are summarized in *Table 8.2.*

Table 8.2	Summary of Environmental Inspections for Contract no. HK/2009/02
-----------	--

ltem	Date	Observations	Action taken by Contractor	Completion date
190124_01	24 January 2019	Dust mitigation shall be enhanced to avoid potential dust emission during breaking and material handling (TWCR4)	Watering was provided to breaking and material handling works	Completed as observed on 24 January 2019

- 8.0.2. Site inspections for Contract no. HY/2009/19 were carried out in the reporting period. No observation was found in the reporting period.
- 8.0.3. Site inspections for Contract no. HK/2012/08 were carried out in the reporting period. The results of these inspections and outcomes are summarized in **Table 8.5**.

## Table 8.5 Summary of Environmental Inspections for Contract no. HK/2012/08

ltem	Date	Observations	Action taken by Contractor	Completion date
190102_1	2 January 2019	Silt / sand deposit around site exit shall clean regularly (Expo Drive)	The sand deposit around site exit was cleaned.	Completion as observed on 8 January 2019
190115_1	15 January 2019	Adequate facilities should be provided for shoe washing to avoid mud being generated out of site area.	Shoe washing facility was installed at site exit	Completion as observed on 22 January 2019

8.0.4. Site inspections for Contract no. HY/2010/08 were conducted in the reporting period. No observation was found in the reporting period.



## 9. Complaints, Notification of Summons and Prosecution

#### 9.0.1. One environmental complaint was received in the reporting period.

An EPD complaint was referred to the ET on 16 January 2019 (CASE Ref: H08/RS/00001488-19, H08/RS/00001532-19, and H08/RS/00001663-19). The complainant reported that milky water discharge was found at the Victoria Harbour, near Causeway Bay Typhoon Shelter on 12 January 2019.

ET confirmed with the WDII Resident Site Staff that the concerned area was located out of the site area of Contract No. HK/2009/02 and the Contractor of HK/2009/02 had no activity at the area concerned on 12 January 2019.

ET confirmed with the CWB Resident Site Staff that no construction works was conducted by the contractor of HY/2010/08 at Victoria Harbour, near Causeway Bay Typhoon Shelter on 12 January 2019 at around noon.

Despite no construction activity was conducted under Contract HK/2009/02 and HY/2010/08 on the concerned date and location as confirmed with corresponding Resident Site Staff, in view of public concern, the Contractor of Contract HK/2009/02 and HY/2010/08 were reminded to review the on-site drainage system and the operation of wastewater treatment system. The Contractor of Contract HK/2009/02 and HY/2010/08 were also reminded to provide mitigation measure such as deployment of silt curtain to enclose the works area if any marine activity to be conducted at the concerned area.

- 9.0.2. The details of cumulative complaint log and updated summary of complaints are presented in Appendix 9.1
- 9.0.3. Cumulative statistic on complaints and successful prosecutions are summarized in *Table 9.1* and *Table 9.2* respectively.

Reporting Period	No. of Complaints
Commencement works (Mar 2010) to last reporting month	49
January 2019	1
Total	50

#### Table 9.1 Cumulative Statistics on Complaints



## Table 9.2 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative No. Project-to-Date
Air	-	0	0
Noise	-	0	0
Water	-	0	0
Waste	-	0	0
Total	-	0	0



Lam Geotechnics Limited

# 10. Conclusion

- 10.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.
- 10.0.2. The scheduled construction activities and the recommended mitigation measures for the coming month are listed in *Table 10.1*.


Contract No.	Key Construction Works	Recommended Mitigation Measures
HK/2009/02	Placing rock armour at TWCR4	<ul> <li>Daily visual inspection of silt screen to ensure the integrity and condition of silt screen.</li> <li>Implement silt screen in accordance with the associated plans submitted to EPD.</li> <li>Ensure proper deployment of silt curtain around marine construction works area.</li> </ul>
HY/2009/19	Seawall block reinstatement     near box culvert T1	Ensure proper deployment of silt curtain around marine construction works area
HK/2012/08	• Nil	• Nil
HY/2010/08	• Nil	• Nil


# Table 10.1Construction Activities and Recommended Mitigation Measures in ComingReporting Month





Figure 2.1

Project Layout

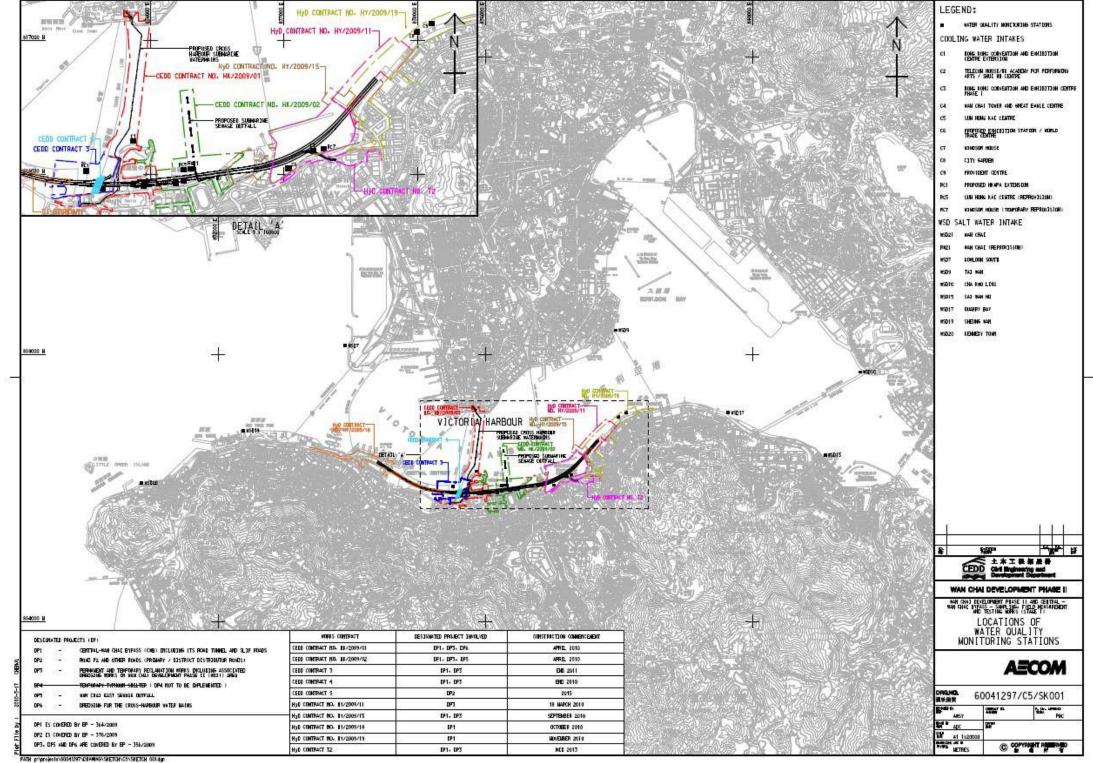


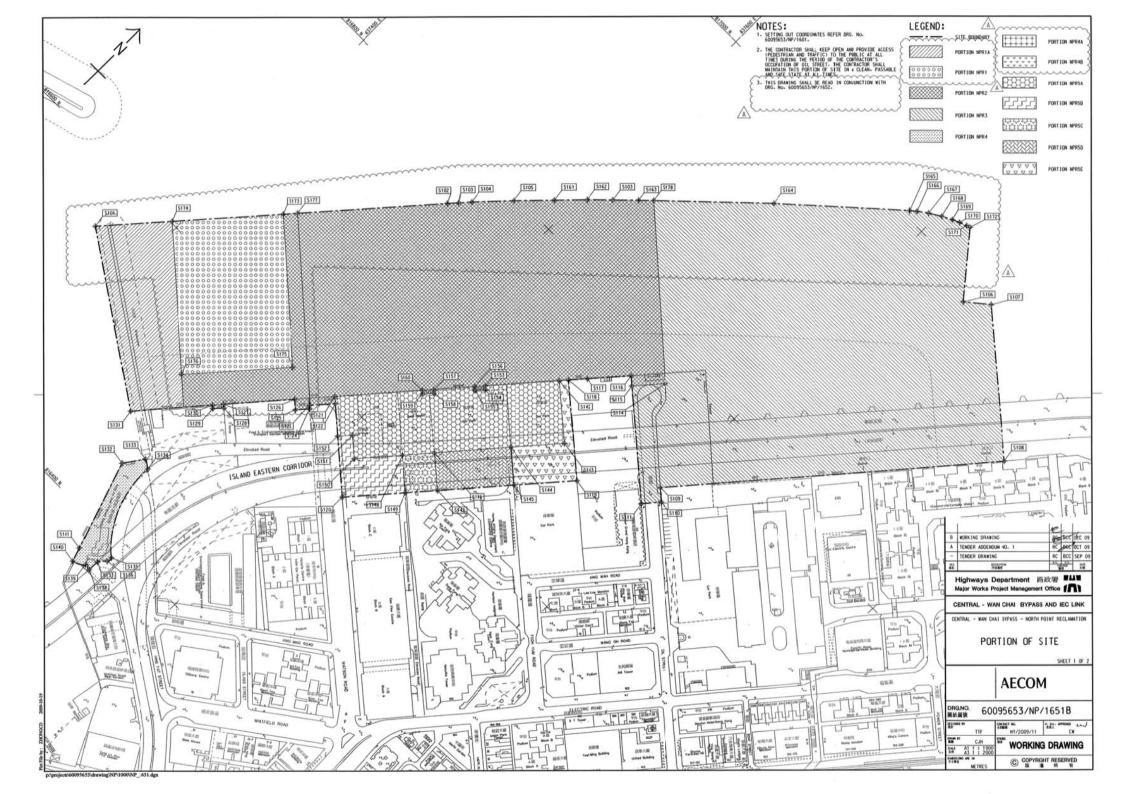


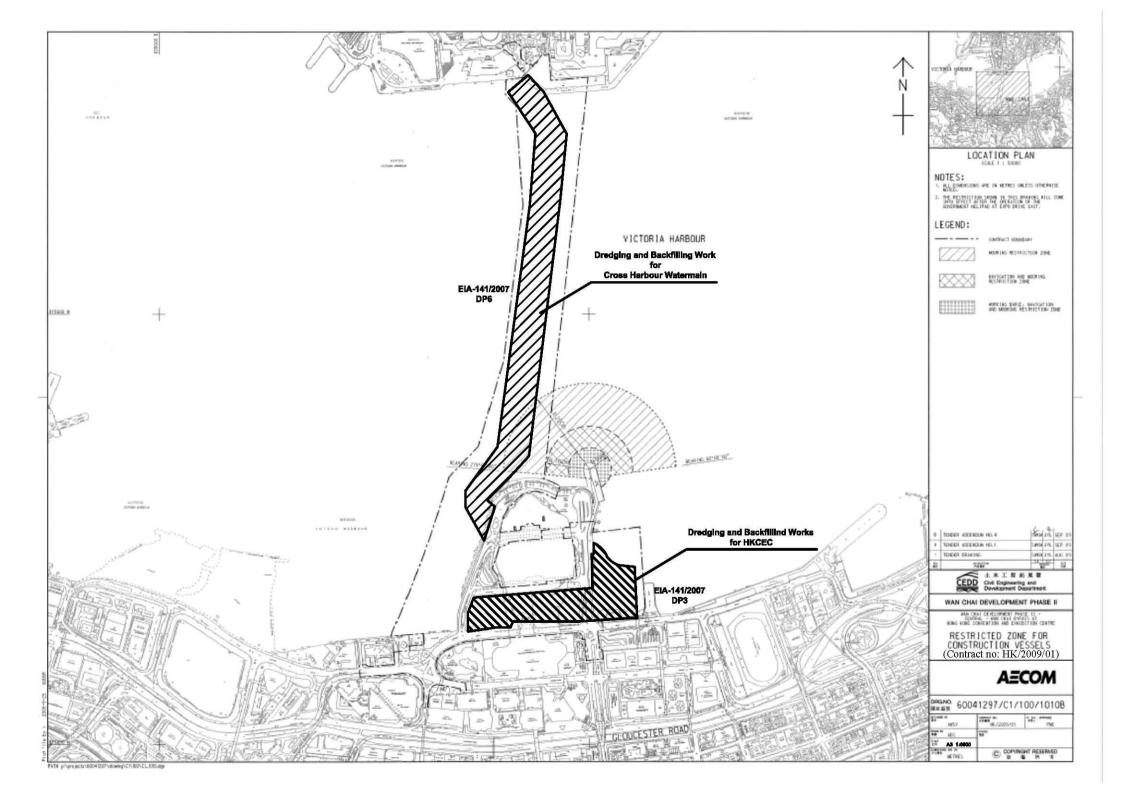


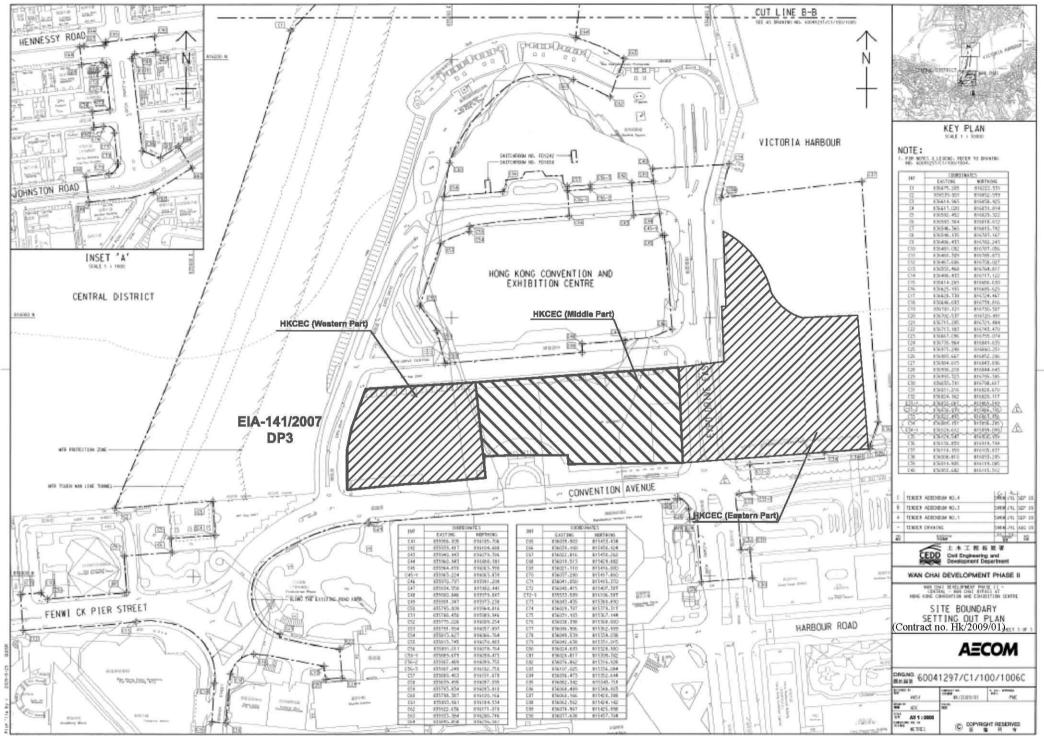


Pate prigratects M0048297 strategy CN 805 CL K86 apr

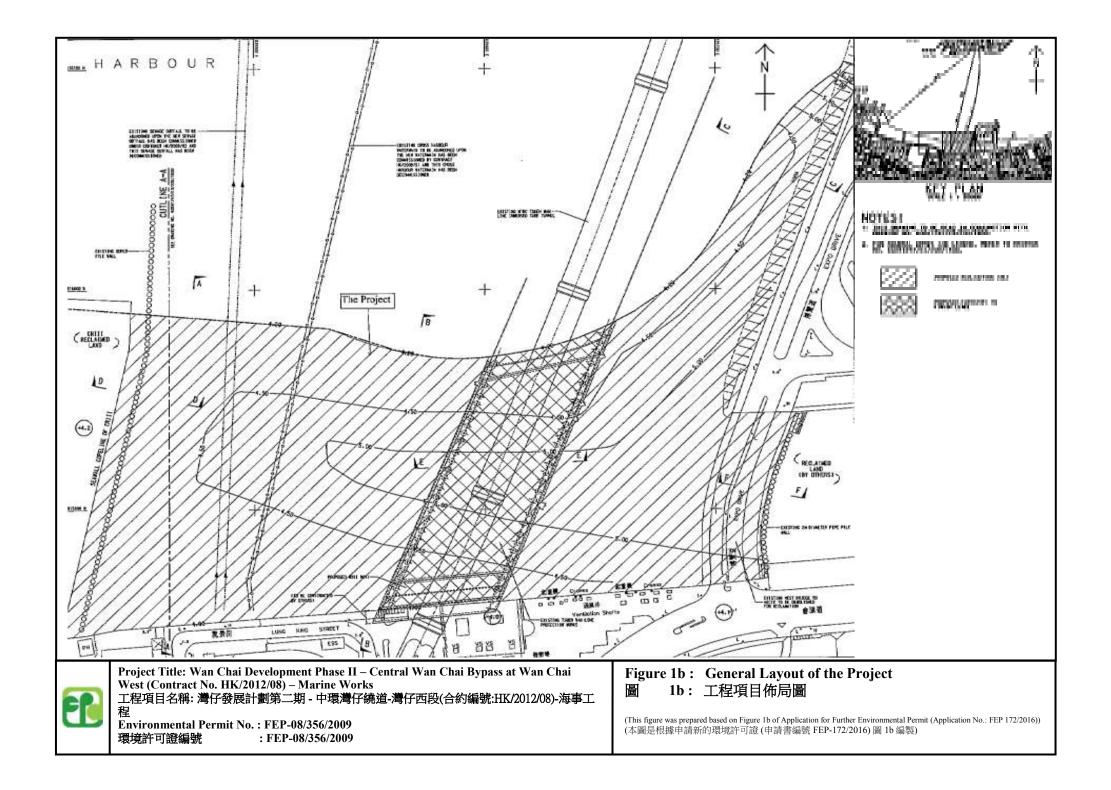

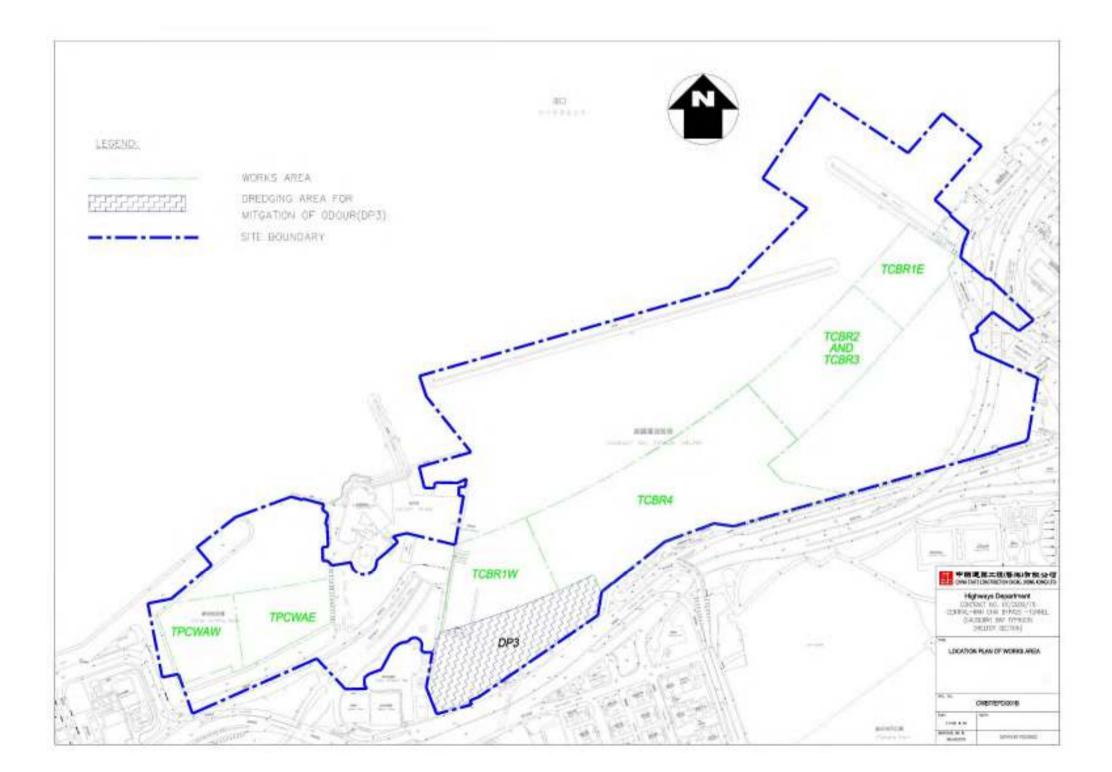

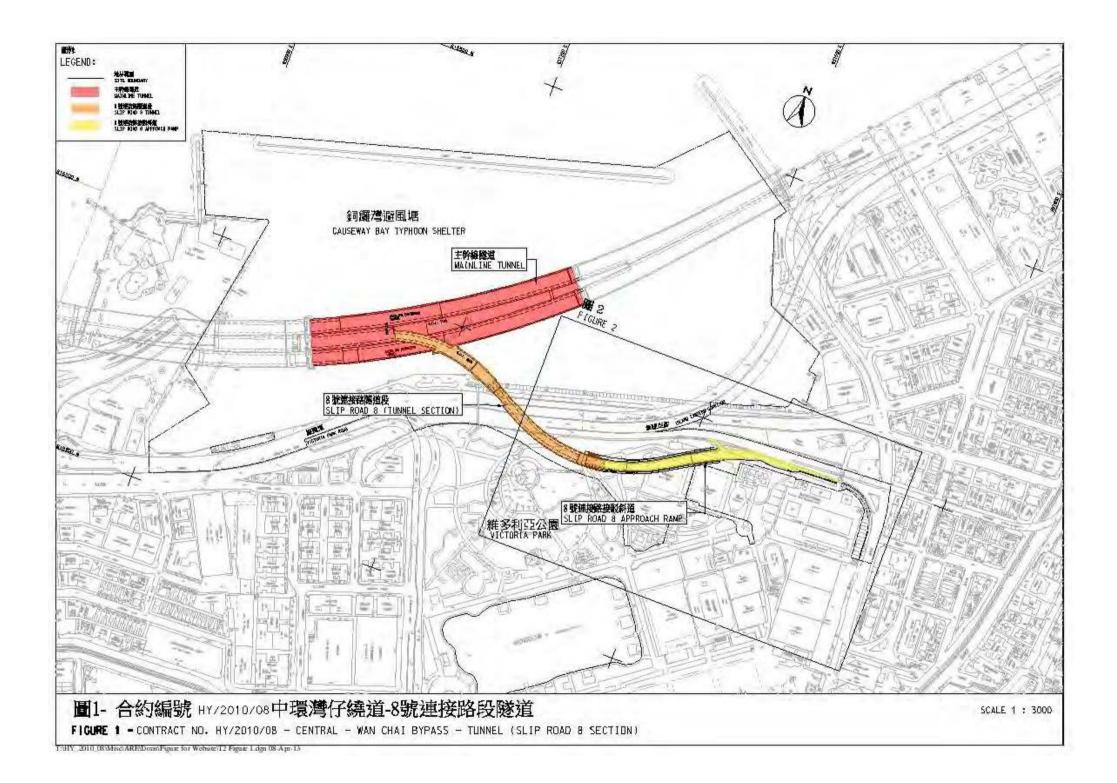

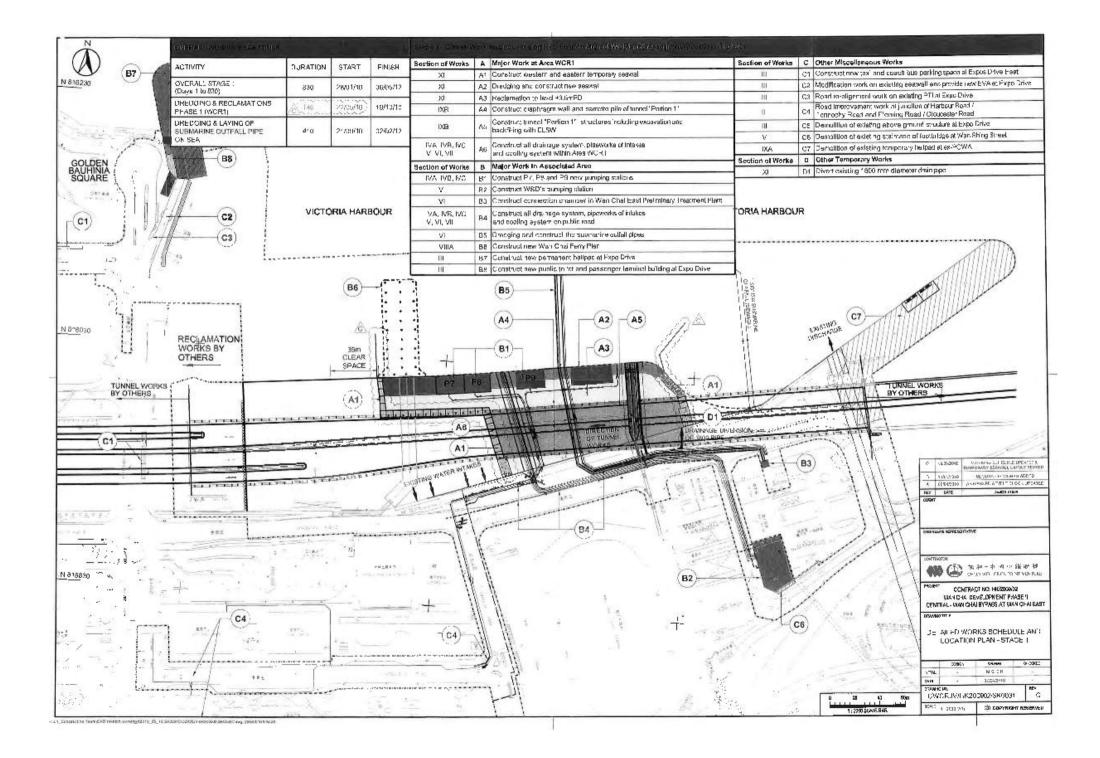

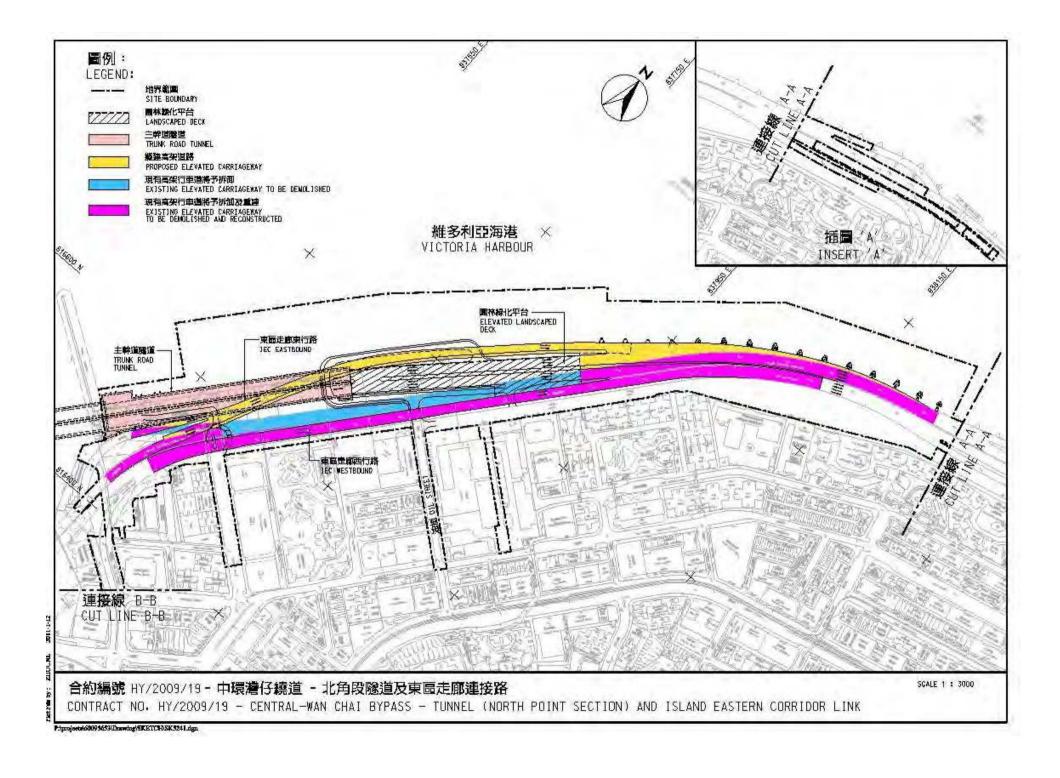




Figure 2.2

**Project Organization Chart** 



## **Project Organization Chart**


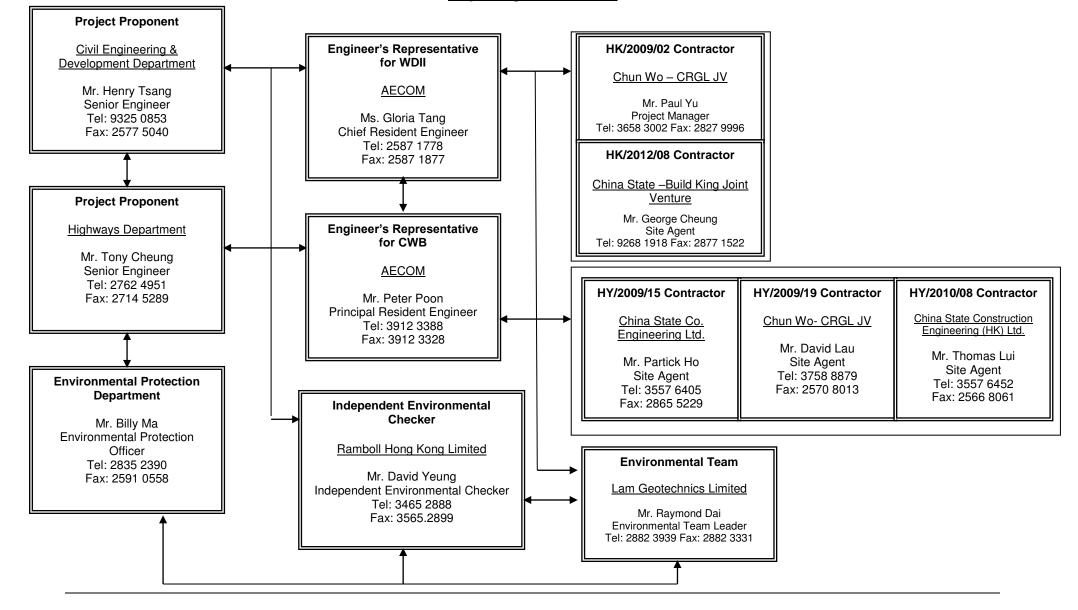




Figure 4.1

## Locations of Monitoring Stations

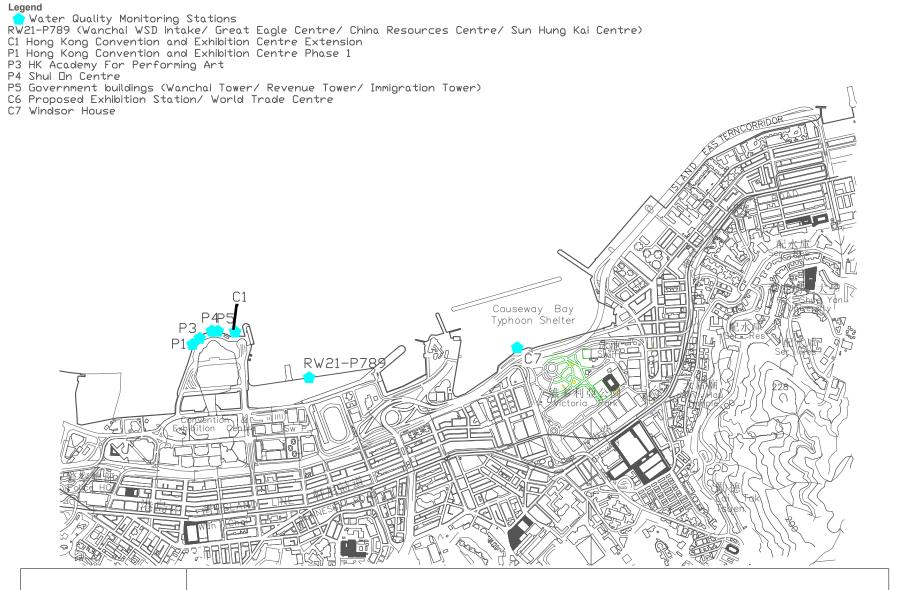



# LOCATIONS OF WATER QUALITY MONITORING STATIONS


**FIGURE** 

#### Legend

Enhance DD Monitoring Stations
 Ex-PCWA SE Ex-Public Cargo Wanchai Area SouthEast Station
 Ex-PCWA SW Ex-Public Cargo Wanchai Area Southwest Station
 C6 Proposed Exhibition Station/ World Trade Centre
 C7 Windsor House

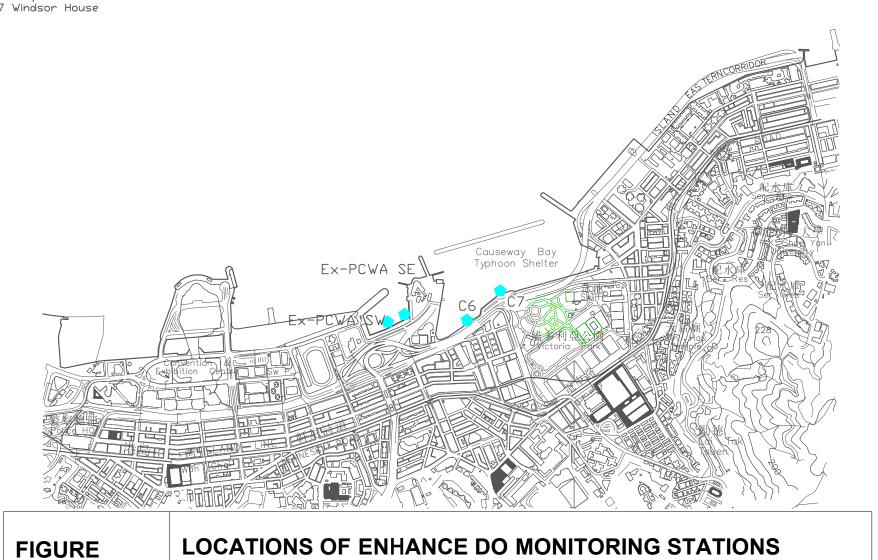

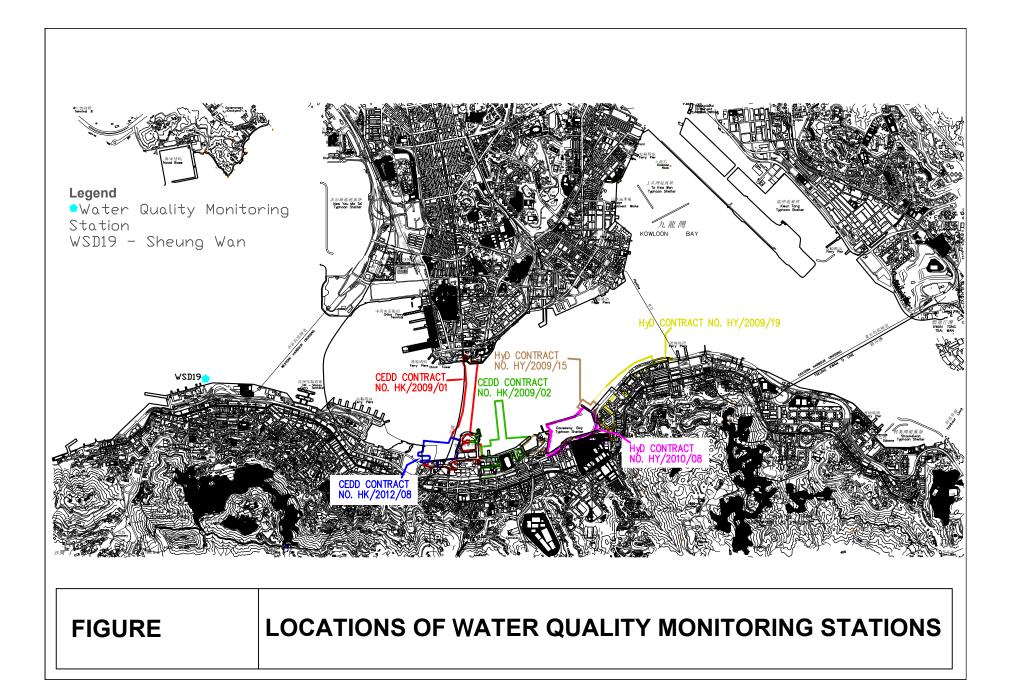

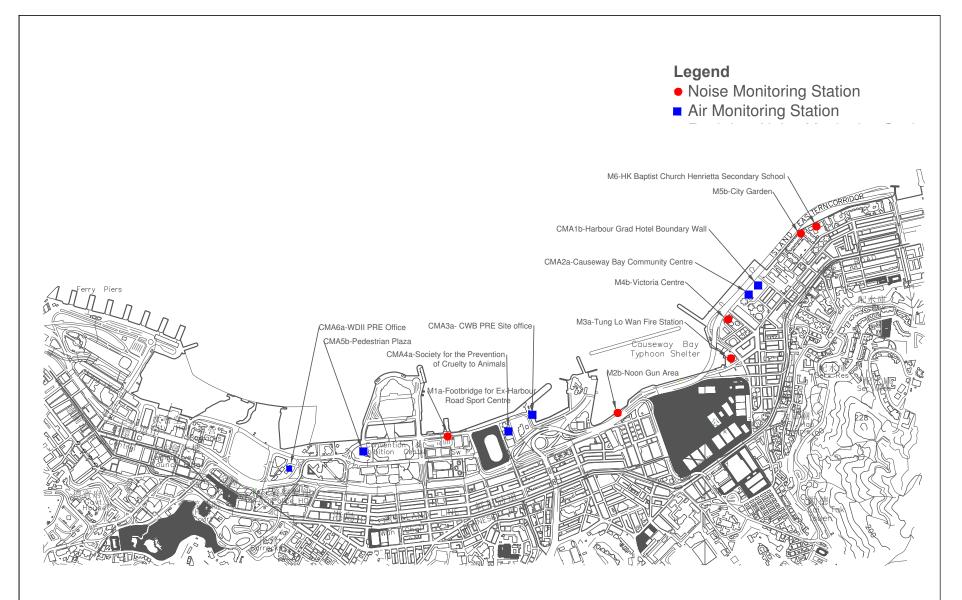

# LOCATIONS OF AIR QUALITY AND NOISE MONITORING STATIONS



Appendix 3.1

Environmental Mitigation Implementation Schedule

Wan Chai Development Phase II and Central-Wanchai Bypass - Sampling, Field Measurement and Testing Works (Stage 3)

Implementation	Schedule	for Air	Ouality	Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	Implementation Stages*			Relevant Legislation
		Docution / Thining	Agent	Des	С	0	Dec	and Guidelines
Constructio								
For the Wh	<i>v</i>		1					1
\$3.6.5	Four times a day watering of the work site with active operations.	Work site / during construction	Contractor		V			EIAO-TM
\$3.8.1	<ul> <li>Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimise cumulative dust impacts.</li> <li>Strictly limit the truck speed on site to below 10 km per hour and water spraying to keep the haul roads in wet condition;</li> <li>Watering during excavation and material handling;</li> <li>Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary; and</li> <li>Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.</li> </ul>	Work site / during construction	Contractor		V			

## Appendix 3.1

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In		entati ges*	on	Relevant Legislation
			Agent	Des	С	0	Dec	and Guidelines
\$3.5.6	For the dredging activities carried out in the vicinity of Police Officers' Club, the dredging operation will be restricted to only I small close grab dredger to minimise the odour impact during the dredging activity. The dredging rate should be reduced as much as practicable for the area in close proximity to the Police Officers' Club. The sediments contain highly contaminated mud which may be disposed with the use of geosynthetic containers (details shall refer to Section 6), grab dredger has to be used for filling up the geosynthetic containers on barges. the dredging rate for the removal of the sediments at the south-west corner of the typhoon shelter shall be slowed down or restricted to specific non-popular hours in weekdays when it is necessary during construction.	Corner of CBTS/implementation of harbour-front enhancement	CEDD <sup>1</sup>		√			EIAO-TM
S3.8.8	Carry out dredging at the corner of CBTS to remove the sediment and clean the slime attached on the CBTS shoreline seawall	Corner of CBTS & CBTS shoreline seawall/implementation of harbour-front enhancement	CEDD <sup>2</sup>		V			EIAO-TM
Operation 1	Phase	1	1					1
For the Wh	ole Project							

<sup>&</sup>lt;sup>1</sup> CEDD will identify an implementation agent.

<sup>&</sup>lt;sup>2</sup> CEDD will identify an implementation agent.

## Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	Implementation Stages*			on	Relevant Legislation
		Liocation, Thing	Agent	Des	С	0	Dec	and Guidelines
\$3.10.2	Monthly (from July to September) monitoring of odour impacts, for a period of 5 years, is proposed during the operational phase of the Project to ascertain the effectiveness of the Enhancement Package over time, and to monitor any on- going odour impacts at the ASRs.	Planned ASRs (CBTS Breakwater)/First 5-year period of operation phase	CEDD <sup>1</sup>			V		EIAO-TM
For DP1 -	CWB (Within the Project Boundary)							
S3.6.53 – S3.6.54	The design parameters of the East and Central Ventilation Buildings as set in Tables 3.10 and 3.11	East and Central Ventilation Buildings / During operation of the Trunk Road	HyD			V		
\$3.10.2	Air quality monitoring for the operation performance of the East Ventilation Building and associated East Vent Shaft will be conducted.	East Vent Shaft / During operation of the East Ventilation Building and associated East Vent Shaft	HyD			V		EIAO-TM

• Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Appendix 3.1

Monthly EM&A Report

Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

 Table A13.2
 Implementation Schedule for Noise Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	In	1 .	entati ges*	on	Relevant Legislation and Guidelines
				Des	С	0	Dec	
Constructio	on Phase							
For the Wh	ole Project							

## Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	Implementation Stages*			on	Relevant Legislation
	Zivitomientai 11000000 Acaba 05 / Aragaton Acaba 05	Docution, Thing	Agent	Des	С	0	Dec	and Guidelines
S4.9.4	<ul> <li>Good Site Practice:</li> <li>Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program.</li> <li>Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program.</li> <li>Mobile plant, if any, shall be sited as far away from NSRs as possible.</li> <li>Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum.</li> <li>Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.</li> <li>Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from onsite construction activities.</li> </ul>	Work Sites / During Construction	Contractor	2.0				EIAO-TM, NCO
For DP1 –	CWB (Within the Project Boundary)							

## Appendix 3.1

Monthly EM&A Report

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	Implementation Stages*			Relevant Legislation
		, <b></b>	Agent	Des	С	0	Dec	and Guidelines
S4.8.3 – S4.8.5	<ul> <li>Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following tasks:</li> <li>Slip road 8 tunnel</li> <li>Construction of diaphragm wall and substructures of the tunnel approach ramp</li> <li>Excavation</li> <li>Construction of slabs</li> <li>Backfill</li> <li>Demolition and construction of substructures for the IEC</li> <li>Demolition works of existing piers and crossheads of the marine section of the existing IEC</li> <li>Use of PME grouping for the following tasks:</li> <li>At-grade road construction</li> <li>Substructure for IECL connection</li> </ul>	Work Sites / During Construction	Contractor		V			EIAO-TM, NCO
For DP2 -	WDII Major Roads (Road P2)							
S4.8.3 – S4.8.4	Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following tasks: • Temporary road diversion • Resurfacing • At-grade roadwork	Work Sites / During Construction	Contractor		V			EIAO-TM, NCO
For DP3 -	Reclamation Works							
S4.8.3 – S4.8.4	Use of quiet powered mechanical equipment for the following task: Filling behind seawall Seawall construction	Work Sites / During Construction	Contractor		V			EIAO-TM, NCO

## Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	nplem Sta	entati ges*	on	Relevant Legislation
LITRO	Environmental Protection Measures / Mugation Measures	Docution / Thining	Agent	Des	С	0	Dec	and Guidelines
For DP5 -	Wan Chai East Sewage Outfall							
S4.8.3 – S4.8.4	Use of quiet powered mechanical equipment for the following tasks: • Submarine pipelines (marine section)	Work Sites / During Construction	Contractor		V			EIAO-TM, NCO
	<ul><li>Use of quiet powered mechanical equipment and movable noise barrier for the following tasks:</li><li>Installation of a new pipeline (land section)</li></ul>							
For DP6 -	Cross-Harbour Water Mains from Wan Chai to Tsim Sha Tsui							
S4.8.3 – S4.8.4	Use of quiet powered mechanical equipment for the following tasks: • Submarine pipelines (marine section) •	Work Sites / During Construction	Contractor		N			EIAO-TM, NCO

## Appendix 3.1

Monthly EM&A Report

Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

 EIA Ref
 Environmental Protection Measures / Mitigation Measures
 Location / Timing
 Implementation Agent
 Implementation Stagests
 Relevant Legislation and Guidelines

 Implementation Measures
 Implementation Measures
 Implementation Agent
 Implementation Measures
 Implementation Agent
 Imple

## Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	nplem Sta	entati ges*	on	Relevant Legislation
		Liocation, Thining	Agent	Des	С	0	Dec	and Guidelines
S4.8.14 - S4.8.18	<ul> <li>For Existing NSRs</li> <li>about 235m length of noise semi-enclosure with transparent panel covering the westbound slip road from the IEC</li> <li>about 230m length of noise semi-enclosure with transparent panel covering the main carriageways (eastbound and westbound) of the CWB and IEC</li> <li>about 135m length of 5.5m high cantilevered noise barrier with 3m cantilever inclined at 45° with transparent panel on the eastbound slip road to the IEC</li> <li>about 95m length of 5.5m high cantilevered noise barrier with 1m cantilever inclined at 45° with transparent panel on the eastbound slip road to the IEC</li> <li>about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC</li> <li>about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC</li> <li>about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC</li> <li>For Noise road surfacing for the trunk road (except tunnel section and beneath the landscaped deck at the eastern portal area) with speed limit of 70 km/hour</li> </ul>	Near North Point / Before commencement of operation of road project	HyD	√ √	√# √	1	Dec	EIAO-TM
	<ul> <li>about 265m length of noise semi-enclosure with transparent panel covering the westbound slip road from the IEC</li> </ul>	Centre (next to City Garden) and CDA(1) site / Before occupation of Planned NSRs in CDA and CDA(1) sites.						

## Appendix 3.1

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	nplem Stag		on	Relevant Legislation	
	-	0	Agent	Agent	Des	С	0	Dec	and Guidelines
	• The openable windows of the temple, if any, should be	Near Causeway Bay Fire	Project						
	orientated so as to avoid direct line of sight to the existing	Station / During detailed	Proponent for						
	Victoria Park Road as far as practicable.	design of the re-	the						
		provisioned Tin Hau	re-provisioned						
		Temple	Tin Hau Temple						

\* Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

<sup>#</sup> Only the steel frame for this section of noise semi-enclosure would be erected in advance during the construction of the westbound slip road.

Wan Chai Development Phase II and Central-Wanchai Bypass - Sampling, Field Measurement and Testing Works (Stage 3)

## Table A13.3 Implementation Schedule for Water Quality Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location /	Implementation	In	plem Stag	entatio ges*	on	Relevant Legislation
		Timing	Agent	Des	С	0	Dec	and Guidelines
Constructio	n Phase							
	Reclamation Works, DP5 (Wan Chai East Sewage Outfall), DP6 (Cross-Harbo	our Water Mains	from Wan Chai to I	sim Sh	a Tsui	i), DP.	1 - CW	B (within the Project
Boundary) S5.8	A phased reclamation approach is planned for the WDII. Containment of fill within each of the reclamation phases by seawalls is proposed, with the seawall constructed first (above high water mark) with filling carried out behind the completed seawalls. Any gaps that may need to be provided for marine access will be shielded by silt curtains to control sediment plume dispersion away from the site. Filling for seawall construction should be carried out behind the silt curtain	Work site / During the construction period	Contractor		V			EIAO-TM, WPCO
S5.8	<ul> <li>Dredging shall be carried out by closed grab dredger for the following works:</li> <li>Seawall construction in all the reclamation areas;</li> <li>Construction of the CWB Tunnel</li> <li>Construction of the proposed WSD water mains; and</li> <li>Construction of the proposed Wan Chai East sewage outfall pipelines.</li> </ul>	Work site / During the construction period	Contractor		V			EIAO-TM, WPCO
\$5.8, Figure 5.3	<ul> <li>Dredging for the Wan Chai East sewage outfall pipelines shall not be carried out concurrently with the following activities:</li> <li>Dredging along the proposed cross-harbour water mains;</li> <li>Dredging along the seawall in the Wan Chai Reclamation (WCR) zone (area between HKCEC Extension and PCWA).</li> </ul>	Work site / During the construction period	Contractor		V			EIAO-TM, WPCO

Appendix 3.1

Monthly EM&A Report

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

EIA Ref	Environmental Protection Measures / I	Mitigation Measures	Location /	Implementation	Ir		entati ges*	on	Relevant Legislation	
		0	Timing	Agent	Des	С	0	Dec	and Guidelines	
\$5.8	The water body behind the temporary rec typhoon shelter shall not be fully enclose		Work site / During the construction period	Contractor		V			EIAO-TM, WPCO	
S5.8	As a mitigation measure, to avoid the acc within the temporary embayment be impermeable barrier, suspended from a and extending down to the seabed, will the HKCEC1 commences. The bar discharge flows from Culvert L to the contractor will maintain this barrier HKCEC2W are carried out and the new 0	etween CRIII and HKCEC1, an floating boom on the water surface be erected by the contractor before rier will channel the stormwater e outside of the embayment. The until the reclamation works in	During the construction period	Contractor		V			EIAO-TM, WPCO	
S5.8, Figure 5.3	The total dredging rates in each of the m than the maximum production rates state production rates without considering the	arine works zones shall not be more ed in the table below. These are the	Work site / During the construction period	Contractor		V			EIAO-TM, WPCO	
	Maximum Dredging Rate         Maximum Dredging           Reclamation Area         m³ per day         m³ per (for 16 hrs per day)         Maximum Predging									
	Dredging along seawall or breakwater           North Point Shoreline Zone (NPR)           Causeway Bay         TBW           Shoreline Zone         TCBR           PCWA Zone         TCBR	6,000         375         42,000           1,500         94         10,500           6,000         375         42,000           5,000         313         35,000								

## Wan Chai Development Phase II and Central-Wanchai Bypass - Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

EIA Ref	Environmental Protection Measure	Environmental Protection Measures / Mitigation Measures		Location /	Implementation	In		entati ges*	on	Relevant Legislation	
LIA KU	Environmental Froteetion Measu	ics/ whileaut	ii wicasui es		Timing	Agent	Des	С	0	Dec	and Guidelines
	Wan Chai Shoreline Zone (WCR)	6,000	375	42,000							
	HKCEC Shoreline Zone HKCEC Stage		94	10,500							
	(HKCEC) HKCEC Stage		375	42,000							
	Cross Harbour Water Mains	1,500	94 94	10,500 10,500							
	Wan Chai East Submarine Sewage Pipeline	1,500	94	10,500							
	Note: 1,500 m <sup>3</sup> per day shall be seawall of WCR1.										
S5.8, Figure 5.3	Dredging along the seawall at 1,500m <sup>3</sup> per day for construction of proximity of the WSD intake), follo western seawall (above high water much as possible from further dredg	of the western wed by partial mark) to pro-	seawall (wh seawall con	tich is in close struction at the	Work site / During the construction period	Contractor		V			EIAO-TM, WPCO
S5.8, Figure 5.3	For dredging within the Causewa partially constructed to protect the dredging activities. For example seawalls shall be constructed firs seawater intakes at the inner water the remaining dredging activities at	at TCBR1W t (above high would be prote	vater intake , the southe water mar cted from th	s from further rn and eastern k) so that the e impacts from	Work site / During the construction period	Contractor		$\checkmark$			EIAO-TM, WPCO
S5.8, Figure 5.3	Silt curtains shall be deployed a seawall dredging and seawall trend TCBR and NP.				Work site / During the construction period	Contractor		$\checkmark$			EIAO-TM, WPCO
S5.8, Figure 5.3	Silt screens shall be applied to seaw as stated below: Interim Construction Locatio	ater intakes at		struction stages	Work site / During the construction	Contractor		$\checkmark$			EIAO-TM, WPCO
	Stage           Scenario         2A in early         WSD s           2009         with concurrent         Bay, Sh           dredging         activities         at         Cooling	altwater intak eung Wan, Wan water intakes	es at Sai Wa Chai, Kowloo for Hong Ko	on South	period						

## Appendix 3.1

Monthly EM&A Report

Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location /	Implementation	In	nplem Stag	entati ges*	on	Relevant Legislation	
			Timing	Agent	Des	С	0	Dec	and Guidelines
	TBW, NP and Water Mains Zone	Convention and Exhibition Centre Phase I, Telecom House / HK Academy for Performing Arts / Shun On Centre, Wan Chai Tower / Revenue Tower / Immigration Tower and Sun Hung Kai Centre							
	Scenario 2B in late 2009/2010 with concurrent dredging activities at Sewage Pipelines Zone and TCBR.	WSD saltwater intakes at Sheung Wan, Wan Chai Cooling water intakes for Queensway Government Offices, Excelsior Hotel, World Trade Centre and Windsor House.							
	Scenario 2C in 2011 with concurrent dredging activities at HKCEC and TCBR.	WSD saltwater intakes at Sheung Wan and Reprovisioned WSD Wan Chai saltwater intake. Cooling water intakes for MTR South, Excelsior Hotel & World Trade Centre and reprovisioned Windsor House.							
\$5.8	spillage and sealed ti	include: used, shall be designed and maintained to avoid ghtly while being lifted. For dredging of any sed watertight grabs must be used;	Work site / During the construction period	Contractor		V			ProPECC PN 1/94; WPCO (TM-DSS)
	vessels and the seabe	d so that adequate clearance is maintained between ed in all tide conditions, to ensure that undue rated by turbulence from vessel movement or							
		dredgers shall be fitted with tight fitting seals to o prevent leakage of material;							
		shall not cause foam, oil, grease, scum, litter or tter to be present on the water within the site or							
	dredged material into t	noppers shall be controlled to prevent splashing of he surrounding water. Barges or hoppers shall not t will cause the overflow of materials or polluted r transportation; and							

## Contract no. HK/2015/01 Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location /	Implementation	In		entati ges*	Relevant Legislation	
		Timing	Agent	Des	С	0	Dec	and Guidelines
	• before commencement of the reclamation works, the holder of Environmental Permit has to submit plans showing the phased construction of the reclamation, design and operation of the silt curtain.							
\$5.8	Silt screens are recommended to be deployed at the seawater intakes during the reclamation works period. Installation of silt screens at the seawater intake points may cause a potential for accumulation and trapping of pollutants, floating debris and refuse behind the silt screens and may lead to potential water quality deterioration at the seawater intake points. Major sources of pollutants and floating refuse include the runoff and storm water discharges from the nearby coastal areas. As a mitigation measure to avoid the pollutant and refuse entrapment problems and to ensure that the impact monitoring results are representative, regular maintenance of the silt screens and refuse collection shall be performed at the monitoring stations at regular intervals on a daily basis. The Contractor shall be responsible for keeping the water behind the silt screen free from floating rubbish and debris during the impact monitoring period.	Work site / During the construction period	Contractor		V			EIAO-TM, WPCO

Appendix 3.1

Monthly EM&A Report

#### Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

Implementation Location / Implementation Relevant Legislation Stages\* EIA Ref **Environmental Protection Measures / Mitigation Measures** Timing and Guidelines Agent Des С 0 Dec S5.8 Dredging of contaminated mud is recommended as a mitigation measures for Causeway Bay  $CEDD^3$ WPCO control of operational odour impact from the Causeway Bay typhoon shelter. typhoon shelter/Imple In recognition of the potential impacts caused by dredging activities close to the seawater intakes, only 1 small close grab dredger shall be operated within mentation of the typhoon shelter (for the dredging to mitigate odour impact) at any time to harbour-front minimize the potential impact. Double silt curtains shall be deployed to fully enhancement. enclose the closed grab dredger during the dredging operation. In addition, an impermeable barrier, suspended from a floating boom on the water surface and extended down to the seabed, shall be erected to isolate the adjacent intakes as much as possible from dredging activities. For example, if dredging is to be carried out at the southwest corner of the typhoon shelter, physical barriers shall be erected to west of the cooling water intake for Excelsior Hotel so that the intake would be shielded from most of the SS generated from the dredging operation to the west of the intake. For area in close proximity of the cooling water intake point, the dredging rate shall be reduced as much as practicable. Site audit and water quality monitoring shall be carried out at the seawater intakes during the dredging operations. Daily monitoring of SS at the cooling water intake shall be carried out, and 24 hour monitoring of turbidity at the intakes shall be implemented during the dredging activities. If the monitoring results indicate that the dredging operation has caused significant changes in water quality conditions at the seawater intakes, appropriate actions shall be taken to stop the dredging and mitigation measures such as slowing down the dredging rate shall be implemented.

Wan Chai Development Phase II and Central-Wanchai Bypass - Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location /	Implementation	Implementation Stages*			on	Relevant Legislation			
LEI KU	2. A Ministra Processin Measures / Minigaton Measures	Timing	Agent	Des	С	0	Dec	and Guidelines			
For the Wh	ole Project										
S5.8	Construction Runoff and Drainage	• Work site	Contractor		$\checkmark$			ProPECC PN 1/94;			
	<ul> <li>use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;</li> </ul>	/ During the constructi on period						WPCO (TM-DSS)			
	<ul> <li>Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94;</li> </ul>	silt 1 of s of			lt						
	<ul> <li>a sediment tank constructed from pre-formed individual cells of approximately 6 - 8 m3 capacity can be used for settling ground water prior to disposal;</li> </ul>										
	<ul> <li>oil interceptors shall be provided in the drainage system for the tunnels and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor shall have a bypass to prevent flushing during periods of heavy rain;</li> </ul>										
	<ul> <li>precautions and actions to be taken when a rainstorm is imminent or forecast, and during or after rainstorms. Particular attention shall be paid to the control of any silty surface runoff during storm events;</li> </ul>										
	<ul> <li>on-site drainage system shall be installed prior to the commencement of other construction activities. Sediment traps shall be installed in order to minimise the sediment loading of the effluent prior to discharge;</li> </ul>										
	<ul> <li>All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge shall be adequately designed for the controlled release of storm flows. All sediment control measures shall be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage shall be reinstated to its original condition when the construction work is finished or the temporary diversion is no longer</li> </ul>										

<sup>3</sup> CEDD will identify an implementation agent.

Appendix 3.1

Monthly EM&A Report

#### Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

Implementation Location / Implementation Relevant Legislation Stages\* EIA Ref **Environmental Protection Measures / Mitigation Measures** Timing and Guidelines Agent Des С 0 Dec required. All fuel tanks and store areas shall be provided with locks and be sited . on sealed areas, within bunds of a capacity equal to 110% of the storage capacity. Minimum distances of 100 m shall be maintained between the storm water discharges and the existing or planned WSD flushing water intakes during construction phase. ProPECC PN 1/94; S5.8 Sewage from Construction Work Force Work site / Contractor V During the WPCO (TM-DSS) Construction work force sewage discharges on site shall be connected to the construction existing trunk sewer or sewage treatment facilities. The construction sewage period shall be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor shall also be responsible for waste disposal and maintenance practices. S5.8 Floating Debris and Refuse WPCO Work site and Contractor λ adjacent water Collection and removal of floating refuse shall be performed at regular intervals on a daily basis. The contractor shall be responsible for keeping the / During the construction water within the site boundary and the neighbouring water free from rubbish. period.

## Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location /	Implementation	Implementation Stages*				Relevant Legislation
	and the second	Timing	Agent	Des	С	0	Dec	and Guidelines
\$5.8	Storm Water Discharges Minimum distances of 100 m shall be maintained between the existing or planned stormwater discharges and the existing or planned WSD flushing water intakes.	Work site and adjacent water / During the design and construction period.	Contractor	V	V			WPCO
Operation	Phase							
	B (within the Project Boundary)	P	-		r	r .		
S5.8	<ul> <li>For the operation of CWB, a surface water drainage system would be provided to collect road runoff. The following operation stage mitigation measures are recommended to ensure road runoff would comply with the TM under the WPCO:</li> <li>The drainage from tunnel sections shall be directed through petrol interceptors to remove oil and grease before being discharged to the nearby foul water manholes.</li> </ul>	CWB/During design and operational period	HyD/TD <sup>3</sup>	V		V		WPCO
	• Petrol interceptors shall be regularly cleaned and maintained in good working condition.							
	Oily contents of the petrol interceptors shall be properly handled and disposed of, in compliance with the requirements of the Waste Disposal Ordinance.							
	• Sewage arising from ancillary facilities of CWB (for examples, car park,							

## Appendix 3.1

Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location /	Implementation	In	nplem Stag	entati ges*	on	Relevant Legislation	
		Gui ann a	Timing	Agent	Des	С	0	Dec	and Guidelines
	•	control room, ventilation and administration buildings and tunnel portals) shall be connected to public sewerage system. Sufficient capacity in public sewerage shall be made available to the proposed facilities. Road drainage shall also be provided with adequately designed silt trap to minimize discharge of silty runoff. The design of the operational stage mitigation measures for CWB shall take into account the guidelines published in ProPECC PN 5/93 "Drainage Plans subject to Comment by the EPD." All operational discharges from the CWB into drainage or sewerage systems are required to be licensed by EPD under the WPCO.							

\* Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

<sup>3</sup> if employ Management, Operation and Maintenance (MOM) Contract

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

## Table A13.4 Implementation Schedule for Waste Management

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	nplem Sta	entati ges*	on	Relevant Legislation
LITRI	Environmental Protection Neusanes / Mitigation Measures	Location / Thining	Agent	Des	С	0	Dec	and Guidelines
Constructio	on Phase							
For DP3 –	Reclamation Works							
	Marine Sediments	Work site / During the construction period	Contractor		V			ETWB TCW No. 34/2002
\$6.7.2	The dredged marine sediments would be loaded onto barges, transported to and disposed of at the designated disposal sites at South of Cheung Chau, East of Ninepin, East of Tung Lung Chau, South of Tsing Yi or East of Sha Chau to be allocated by the MFC depending on their level of contamination or at other disposal sites after consultation with the MFC and EPD. In accordance with the ETWB TCW No. 34/2002, the contaminated material must be dredged and transported with great care. The mitigation measures recommended in Section 5 of the EIA Report shall be incorporated. The dredged contaminated sediment must be effectively isolated from the environment upon final disposal and shall be disposed of at the Type 2 confined marine disposal contaminated mud pit.							
86.7.3	Based on the biological screening results, the Category H (>10xLCEL) sediment which failed the biological testing would require Type 3 special disposal. The volume of Category H sediment from the Causeway Bay typhoon shelter which would require special disposal arrangements is estimated to be approximately 0.05 Mm <sup>3</sup> . A feasible containment method is proposed whereby the dredged sediments are sealed in geosynthetic containers and, at the disposal site, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping, thereby meeting the requirements for fully confined mud disposal.							

## Appendix 3.1

Monthly EM&A Report

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	ıplem Staş	entati ges*	on	Relevant Legislation
			Agent	Des	С	0	Dec	and Guidelines
S6.7.5	It will be the responsibility of the Contractor to satisfy the appropriate authorities that the contamination levels of the marine sediment to be dredged have been analysed and recorded. According to the ETWB TCW No. 34/2002, this will involve the submission of a formal Sediment Quality Report to the DEP, at least 3 months prior to the dredging contract being tendered							
S6.7.6	<ul> <li>During transportation and disposal of the dredged marine sediments requiring Type 1 and Type 2 disposal, the following measures shall be taken to minimise potential impacts on water quality:</li> <li>Bottom opening of barges shall be fitted with tight fitting seals to prevent leakage of material. Excess material shall be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.</li> </ul>							

## Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In		entati ges*	on	Relevant Legislation
		Location, Thing	Agent	Des	С	0	Dec	and Guidelines
	<ul> <li>Monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the DEP.</li> <li>Barges or hopper barges shall not be filled to a level that would cause the overflow of materials or sediment laden water during loading or transportation.</li> </ul>							
\$6.6.12	<i>Floating Refuse</i> During the construction phase, the project proponent's contractor will be responsible for the collection of any refuse within their works area. Floating booms will be provided on the water surface to confine the refuse from the working barges as well as to avoid the accumulation of pollutants within temporary embayment as mentioned in Table 13.3.	Work site / During the construction period	Contractor		V			

For the Whole Project

Appendix 3.1

Monthly EM&A Report

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In		entati ges*	on	Relevant Legislation
	and the second sec		Agent	Des	С	0	Dec	and Guidelines
S6.7.7	<ul> <li>Good Site Practices</li> <li>Recommendations for good site practices during the construction activities include:</li> <li>nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site;</li> <li>training of site personnel in proper waste management and chemical waste handling procedures;</li> <li>provision of sufficient waste disposal points and regular collection for disposal;</li> <li>appropriate measures to minimise windblown litter and dust during transporting wastes in enclosed containers;</li> <li>regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and</li> <li>a recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).</li> </ul>	Work site / During the construction period	Contractor	Des		0	Dec	Waste Disposal Ordinance (Cap.354)

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In		entati ges*	ion	Relevant Legislation
	Environmental Protection Measures / Mitagaton Measures	Docution / Thining	Agent	Des	С	0	Dec	and Guidelines
S6.7.8	<ul> <li>Waste Reduction Measures</li> <li>Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</li> <li>segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> </ul>	Work site / During planning and design stage, and construction stage	Contractor	V	V			
	<ul> <li>to encourage collection of aluminium cans, PET bottles and paper, separate labelled bins shall be provided to segregate these wastes from other general refuse generated by the work force;</li> </ul>							
	• any unused chemicals or those with remaining functional capacity shall be recycled;							
	<ul> <li>use of reusable non-timber formwork, such as in casting the tunnel box sections, to reduce the amount of C&amp;D material.</li> </ul>							
	<ul> <li>prior to disposal of C&amp;D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill;</li> </ul>							
	• proper storage and site practices to minimise the potential for damage or contamination of construction materials; and							
	<ul> <li>plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.</li> </ul>							

## Appendix 3.1

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	nplem Sta	entati ges*	on	Relevant Legislation
	g		Agent	Des	С	0	Dec	and Guidelines
S6.7.10	General Refuse General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D material. A collection area shall be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind blow' light material.	Work site / During the construction period	Contractor		V			Public Health and Municipal Services Ordinance (Cap. 132)
\$6.7.11	Chemical Wastes After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals shall be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work site / During the construction period	Contractor		V			Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
\$6.7.12	Construction and Demolition Material C&D material shall be sorted on-site into inert C&D material (that is, public fill) and C&D waste. All the suitable inert C&D material shall be broken down to 250 mm in size for reuse as public fill in the WDII reclamation. C&D waste, such as wood, glass, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials.	Work site / During the construction period	Contractor		V			ETWB TCW No. 33/2002, 31/2004, 19/2005

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	nplem Sta	entati ges*	on	Relevant Legislation
LINKI	Environmental Protection Measures / Mitagation Measures	Location / Thining	Agent	Des	С	0	Dec	and Guidelines
\$6.7.13	In order to monitor the disposal of public fill and C&D waste at public filling facilities and landfills, respectively, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team undertaking the environmental monitoring and audit work. An Independent Environment Checker shall be responsible for auditing the results of the system.	Work site / During the construction period	Contractor and Independent Environmental Checker		V			ETWB TCW No. 31/2004
\$6.7.14	<ul> <li>Bentonite Slurry</li> <li>The disposal of residual used bentonite slurry shall follow the good practice guidelines stated in ProPECC PN 1/94</li> <li>"Construction Site Drainage" and listed as follows:</li> <li>If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis.</li> </ul>	Work site / During the construction period	Contractor		V			ProPECC PN 1/94
	• If the used bentonite slurry is intended to be disposed of through the public drainage system, it shall be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the Technical Memorandum of Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters.							
	<ul> <li>If the used bentonite slurry is intended to be disposed to public fill reception facilities, it will be mixed with dry soil on site before disposal.</li> </ul>							

\* Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Appendix 3.1

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

## Table A13.5 Implementation Schedule for Land Contamination

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In		entati ges*	on	Relevant Legislation
Lint Ker	Environmental Protection Measures / Mitigation Measures	Location / Timing	Agent	Des	С	0	Dec	and Guidelines
Constructio	on Phase							
For the Wh	ole Project							
S.12.6	• The contaminated site shall be cleaned up before commencement of site clearance and construction work at the concerned area which may disturb the ground.	A King Marine / Before commencement of construction activities at A King Marine.	Project proponent for the re- provisioned Tin Hau Temple	V				"Guidance Notes for Investigation and Remediation of Contaminated Sites of Petrol Filling Stations, Boatyards, and Car Repair/Dismantling Workshops" published by EPD, HKSAR EPD ProPECC Note No. 3/94
\$7.10	<ul> <li>During soil remediation works, the Contractor for the excavation works shall take note of the following points for excavation:</li> <li>Excavation profiles must be properly designed and executed;</li> <li>In case the soil to be excavated is situated beneath the groundwater table, it may be necessary to lower the groundwater table by installing well points or similar means;</li> <li>Quantities of soil to be excavated must be estimated;</li> <li>It maybe necessary to split quantities of soil according to soil type, degree and nature of contamination.</li> <li>Temporary storage of soil at intermediate depot or on-site</li> </ul>	A King Marine / During soil remediation works	Contractor	V				Air Pollution Control Ordinance Noise Control Ordinance Waste Disposal Ordinance Waste Disposal (Chemical Waste) (General) Regulation

## Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	In	nplem Sta	entati ges*	on	Relevant Legislation
				Des	С	0	Dec	and Guidelines
	maybe required. The storage site shall include protection facilities for leaching into the ground. eg. Liner maybe required.							
	<ul> <li>Supply of suitable clean backfill materials is needed after excavation.</li> <li>Care must be taken of existing buildings and utilities.</li> <li>Precautions must be taken to control of ground settlement</li> <li>Speed controls for vehicles shall be imposed on dusty site areas.</li> <li>Vehicle wheel and body washing facilities at the site's exit points shall be established and used.</li> <li>The following environmental mitigation measures shall be strictly followed during the operation and/or maintenance of the CS/S facilities:</li> </ul>							Water Pollution Control Ordinance

Appendix 3.1

Monthly EM&A Report

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	nplem Sta	entati ges*	Relevant Legislation	
	5	0	Agent	Des	С	0	Dec	and Guidelines
	<ul> <li><u>Air Quality Mitigation Measures</u></li> <li>The loading, unloading, handling, transfer or storage of cement shall be carried out in an enclosed system.</li> <li>The loading, unloading, handling, transfer or storage of other materials which may generate airborne dust emissions such as untreated soil and oversize materials sorted out from the screening plant and stabilized soil stockpiled in the designated handling area, shall be carried out in such a manner to prevent or minimise dust emissions. These materials shall be adequately wetted prior to and during the loading, unloading and handling operations.</li> <li>All practicable measures, including speed controls for vehicles, shall be taken to prevent or minimize the dust emission caused by vehicle movement.</li> <li>Tarpaulin or low permeable sheet shall be put on dusty vehicle loads transported between site locations.</li> </ul>							
	<ul> <li><u>Noise Mitigation Measures</u></li> <li>The mixing facilities shall be sited as far as practicable to the nearby noise sensitive receivers.</li> <li>Simultaneous operation of mixing facilities and other equipment shall be avoided.</li> <li>Mixing process and other associated material handling activities shall be properly scheduled to minimise potential cumulative noise impact on the nearby noise sensitive receivers.</li> <li>Construction Noise Permit shall be applied for the operation of powered mechanical equipment during restricted hours (if any).</li> </ul>							

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	In	nplem Stag	entati ges*	on	Relevant Legislation
				Des	С	0	Dec	and Guidelines
	Water Quality Mitigation Measures							
	• Stockpile of untreated soil shall be covered as far as practicable to prevent the contaminated material from							
	leaching out. The leachate shall be discharged following the requirements of WPCO.							
	Waste Mitigation Measures							
	• Treated oversize materials will be used as filling material							
	for backfilling within the site. Sorted materials of size smaller than 5 cm will be collected and transferred to the							
	mixing plant for further decontamination treatment.							
	<ul> <li>Stabilized soils shall be broken into suitable size for backfilling or reuse on site.</li> </ul>							
	• A high standard of housekeeping shall be maintained within the mixing plant area.							
	<ul> <li>If necessary, there shall be clear and separated areas for stockpiling of untreated and treated materials.</li> </ul>							

\* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Appendix 3.1

Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

## Table A13.6 Implementation Schedule for Marine Ecology

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation
				Des	С	0	Dec	and Guidelines
Constructio	on Phase							
For the Wh	ole Project - Schedule 3 DP							
S.9.7.2	Alternative design of the Trunk Road constructed in tunnel shall be adopted to avoid permanent reclamation in CBTS and ex-PWCA Basin.	-	CEDD/HyD	V				EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
For DP3 –	Reclamation Works							
S.9.7.3	Translocation of those potentially affected coral colonies to the nearby suitable habitats such as Junk Bay is recommended. A detailed translocation plan (including translocation methodology, monitoring of transplanted corals, etc.) should be drafted and approval by AFCD during the detailed design stage of the Project.	Ex-PCWA Basin and along seawall next to a public pier which is about 250 m away from the CBTS	CEDD/HyD	V				EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.

## Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In		entati ges*	on	Relevant Legislation
		Location, Thing	Agent	Des	С	0	Dec	and Guidelines
S.9.7.4	<ul> <li>During dredging and filling operations, a number of mitigation measures to control water quality shall be adopted to confine sediment plume within reclamation area and protect marine fauna in proximity to the reclamation. The mitigation measures include the following:</li> <li>Installation of silt curtains during dredging activities</li> <li>Use of tightly-closed grab dredger</li> <li>Reduction of dredging rate</li> <li>Control of grab descending speed</li> <li>Construction of leading edges of seawall in the early stages of the reclamation works</li> </ul>	Work site / during construction phase	Contractor		~			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
	Adoption of multiple-phase construction schedule							

Appendix 3.1

Monthly EM&A Report

Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	Implementation Stages*			on	Relevant Legislation
	g		Agent	Des	С	0	Dec	and Guidelines
S.9.7.6	<ul> <li>To minimize potential disturbance impacts on the foraging ardeid population in the CBTS, particularly in the area near the A King Shipyard, appropriate mitigation measures shall be adopted particularly during the construction phase. The following measures are recommended:</li> <li>Use of Quiet Mechanical Plant during the construction phase shall be adopted wherever possible.</li> <li>Adoption of multiple-phase construction schedule.</li> <li>General measures to reduce noise generated during the construction phase (see noise impact assessment) shall be effectively implemented.</li> </ul>	Work site / during construction phase	Contractor		V			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
S.9.7.7	Seawalls shall be constructed in advance around the reclamation areas within the area of the CBTS to screen adjacent feeding ground from construction phase activities, reduce noise disturbance to the associated seabirds and also to restrict access to this habitat adjacent to works areas by ship traffic.	Work site / during construction phase	Contractor		~			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
S.9.7.8	Loss of artificial seawall habitats shall be reinstated by the construction of about 1 km vertical wave absorbing seawall along the coastlines of the new reclamation around the HKCEC and at North Point. The new seawalls are expected to provide large area of hard substrata for settlement and recruitment of intertidal fauna similar to those previously recorded from existing intertidal habitats.	Work site / during construction phase	Contractor		V			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.

\*Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

## Table A13.7 Implementation Schedule for Landscape and Visual

EIA Ref	Environme	ental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				0	Des	С	0	Dec	
Construction	Phase					I		1	
For the Whole	Project								
Table 10.5	re-u	psoil, where identified, shall be stripped and stored for use in the construction of the soft landscape works, ere practical.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5		isting trees to be retained on site shall be carefully tected during construction.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5		es unavoidably affected by the works shall be nsplanted where practical.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5		mpensatory tree planting shall be provided to mpensate for felled trees.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5	CM5 Con	ntrol of night-time lighting.	Work site / During Construction Phase	Contractor		V			EIAO TM
Table 10.5		ection of decorative screen hoarding compatible with surrounding setting.	Work site / During Construction Phase	Contractor		V			EIAO TM
For DP1 - CV	VB (Within th	he Project Boundary)							
Table 10.5	re-u whe	osoil, where identified, shall be stripped and stored for use in the construction of the soft landscape works, ere practical.	Work site / During Construction Phase	Contractor		V			EIAO TM
Table 10.5		isting trees to be retained on site shall be carefully tected during construction.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5		es unavoidably affected by the works shall be nsplanted where practical.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5		mpensatory tree planting shall be provided to npensate for felled trees.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5	CM5 Con	trol of night-time lighting.	Work site / During Construction Phase	Contractor		V			EIAO TM

Appendix 3.1

Monthly EM&A Report

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

EIA Ref	Envir	onmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
					Des	С	0	Dec	
Table 10.5	CM6	Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		V			EIAO TM
For DP2 - WD	II Majo	r Roads (Road P2)							
Table 10.5	CM1	Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5	CM2	Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5	CM3	Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5	CM4	Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5	CM5	Control of night-time lighting.	Work site / During Construction Phase	Contractor		V			EIAO TM
Table 10.5	CM6	Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		V			EIAO TM
For DP3 – Rec	lamatio	n Works							
Table 10.5	CM5		Work site / During Construction Phase	Contractor		$\checkmark$			EIAO TM
Table 10.5	CM6	Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		$\checkmark$			EIAO TM
For DP5 - Wat	ı Chai I	East Sewage Outfall							
Refer to EIA- 058/2001 Table 10.13	CM2	Minimisation of works areas.	Work site / During Construction Phase	Contractor		V			EIAO TM
Refer to EIA- 058/2001 Table 10.13	CM3	Erection of decorative hoardings.	Work site / During Construction Phase	Contractor		V			EIAO TM

Wan Chai Development Phase II and Central-Wanchai Bypass - Sampling, Field Measurement and Testing Works (Stage 3)

Monthly EM&A Report

EIA Ref	Envir	onmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
					Des	С	0	Dec	
Refer to EIA- 058/2001 Table 10.13	CM4	Control night-time lighting.	Work site / During Construction Phase	Contractor		V			EIAO TM
Refer to EIA- 058/2001 Table 10.13	CM5	Minimisation of disruption to public by effective programming of the works.	Work site / During Construction Phase	Contractor		V			EIAO TM
	ss-Harh	our Water Mains from Wan Chai to Tsim Sha Tsui						1	
Refer to EIA- 058/2001 Table 10.13		Minimisation of works areas.	Work site / During Construction Phase	Contractor		V			EIAO TM
Refer to EIA- 058/2001 Table 10.13	CM3	Erection of decorative hoardings.	Work site / During Construction Phase	Contractor		V			EIAO TM
Refer to EIA- 058/2001 Table 10.13	CM4	Control night-time lighting.	Work site / During Construction Phase	Contractor		V			EIAO TM
Refer to EIA- 058/2001 Table 10.13	CM5	Minimisation of disruption to public by effective programming of the works.	Work site / During Construction Phase	Contractor		V			EIAO TM
<b>Operation Pha</b>									
	Project	- Schedule 3 DP							
Table 10.6, Figure 10.5.1- 10.5.5	OM1	Aesthetic design of buildings and road-related structures, including viaducts, vent buildings, subways, footbridges and noise barriers and enclosure.	Work site / During Design Stage and Operation Phases	CEDD/HyD	V	V			ETWB TCW 2/2004
Table 10.6, Figure 10.5.1- 10.5.5	OM2	Shrub and Climbing Plants to soften proposed structures.	Work site / During Design Stage and Operation Phases	CEDD/HyD	$\checkmark$	V	V		ETWB TCW 2/2004

## Appendix 3.1

Monthly EM&A Report

## Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Enviro	nmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	In	nplem Sta	entati ges*		Relevant Legislation and Guidelines
					Des	С	0	Dec	
Table 10.6,	OM3	Buffer Tree and Shrub Planting to screen proposed roads	Work site / During	CEDD/HyD/					ETWB TCW 2/2004
Figure 10.5.1-		and associated structures.	Design Stage and						
10.5.5			Operation Phases						
Table 10.6,	OM4	Aesthetic design of proposed waterfront promenade.	Work site / During	$CEDD^4$					ETWB TCW 2/2004
Figure 10.5.1-			Design Stage and						
10.5.5			Operation Phases						
Table 10.6,	OM5	Aesthetic streetscape design.	Work site / During	CEDD/HyD			V		ETWB TCW 2/2004
Figure 10.5.1-			Design Stage and						
10.5.5			Operation Phases						
Table 10.6,	OM6	Aesthetic design of roadside amenity areas.	Work site / During	CEDD/HyD	$\checkmark$				ETWB TCW 2/2004
Figure 10.5.1-			Design Stage and						
10.5.5			Operation Phases						
		n the Project Boundary)	1	T					
Table 10.6,	OM1	Aesthetic design of buildings and road-related structures,	Work site / During	HyD					ETWB TCW 2/2004
Figure 10.5.1-		including viaducts, vent buildings, subways, footbridges	Design Stage and						
10.5.5		and noise barriers and enclosure.	Operation Phases						
Table 10.6,	OM2	Shrub and Climbing Plants to soften proposed structures	Work site / During	HyD					ETWB TCW 2/2004
Figure 10.5.1-			Design Stage and						
10.5.5			Operation Phases		,				
Table 10.6,	OM3	Buffer Tree and Shrub Planting to screen proposed roads	Work site / During	HyD	$\checkmark$		$\checkmark$		ETWB TCW 2/2004
Figure 10.5.1-		and associated structures.	Design Stage and						
10.5.5			Operation Phases						
Table 10.6,	OM5	Aesthetic streetscape design.	Work site / During	HyD		V	$\checkmark$		ETWB TCW 2/2004
Figure 10.5.1-			Design Stage and						
10.5.5	0144		Operation Phases			1			
Table 10.6,	OM6	Aesthetic design of roadside amenity areas.	Work site / During	HyD	$\checkmark$	V	$\checkmark$		ETWB TCW 2/2004
Figure 10.5.1-			Design Stage and						
10.5.5			Operation Phases						
For DP2 - WD	I Major	Roads (Road P2)							

<sup>4</sup> CEDD will identify an implementation agent

Wan Chai Development Phase II and Central-Wanchai Bypass

- Sampling, Field Measurement and Testing Works (Stage 3)

EIA Ref	Envir	onmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
					Des	С	0	Dec	
Table 10.6, Figure 10.5.1- 10.5.5	OM1	Aesthetic design of buildings and road-related structures, including viaducts, vent buildings, subways, footbridges and noise barriers and enclosure.	Work site / During Design Stage and Operation Phases	CEDD/HyD		V	V		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1- 10.5.5	OM3	Buffer Tree and Shrub Planting to screen proposed roads and associated structures.	Work site / During Design Stage and Operation Phases	CEDD/HyD		V	V		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1- 10.5.5	OM5	Aesthetic streetscape design.	Work site / During Design Stage and Operation Phases	CEDD/HyD		V	V		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1- 10.5.5	OM6	Aesthetic design of roadside amenity areas	Work site / During Design Stage and Operation Phases	CEDD/HyD		V	V		ETWB TCW 2/2004
For DP3 - Rec				-				1	
Table 10.6, Figure 10.5.1- 10.5.5	OM4	Aesthetic design of proposed waterfront promenade.	Work site / During Design Stage and Operation Phases	CEDD <sup>5</sup>	V	V	V		ETWB TCW 2/2004

\*Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

 $^5$  CEDD will identify an implementation agent

Appendix 3.1



Appendix 4.1

Action and Limit Level



Lam Geotechnics Limited

## Action and Limit Level

## Action and Limit Level for Noise Monitoring

Time Period	Action Level	Limit Level
07:00 – 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A) <sup>Note 1</sup>

Note 1:

- 70dB(A) and 65 dB(A) for schools during normal teaching periods and school examination periods, respectively.

- If works are to be carried out during the restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

## Action and Limit Level for Air Quality Monitoring

Monitoring Location	1-hour TSP Level in $\mu$ g/m <sup>3</sup>		24-hour TSP Level in $\mu$ g/m <sup>3</sup>			
	Action Level	Limit Level	Action Level	Limit Level		
CMA1b	320.1	500	176.7	260		
CMA2a	323.4	500	169.5	260		
CMA3a	311.3	500	171.0	260		
CMA4a	312.5	500	171.2	260		
CMA5b	332.0	500	181.0	260		
CMA6a	300.1	500	187.3	260		

## Action and Limit Level for Water Quality Monitoring

Parameters	Dry S	eason	Wet Season						
Parameters	Action Limit		Action	Limit					
WSD Salt Water Intake									
SS in mg L <sup>-1</sup>	13.00	14.43	16.26	19.74					
Turbidity in NTU	8.04	9.49	10.01	11.54					
DO in mg/L	3.66	3.28	3.17	2.63					
Cooling Water Intal	(e								
SS in mg L <sup>-1</sup>	15.00	22.13	18.42	27.54					
Turbidity in NTU	9.10	10.25	11.35	12.71					
DO in mg/L	3.36	2.73	3.02	2.44					

Remarks:

- Action and Limit Level for the wet season are applied after the EPD approval of Updated EM&A Manual on 29 April 2011.

## Action and Limit Level for Enhance DO Monitoring

Parameters	Depth	Dry Season		Wet Season		
Parameters		Action	Limit	Action	Limit	
C6	Surface and Middle	3.13	2.00	2.60	2.00	
0	Bottom	4.14	3.33	2.91	2.34	
C7	Surface and Middle	3.87	3.09	3.31	2.57	
07	Bottom	3.91	3.53	2.75	2.48	
Ex-WPCWA SW	Surface and Middle	3.84	3.73	3.19	3.10	
EX-WEGWA SW	Bottom	4.71	4.63	3.31	3.25	
	Surface and Middle	4.26	3.61	3.55	3.00	
Ex-WPCWA SE	Bottom	5.36	5.35	3.76	3.76	

## Action and Limit Levels for Odour Patrol

Parameters	Action	Limit			
Odour Nuisance (from odour intensity analysis or odour patrol)	<ul> <li>When two documented complaint are received; or</li> <li>Odour Intensity of 2 is measured from odour intensity analysis.</li> </ul>	<ul> <li>Five or more consecutive genuine documented complaints within a week; or</li> <li>Odour Intensity of 3 or above is measured from odour intensity analysis.</li> </ul>			



Appendix 4.2

**Copies of Calibration Certificates** 

15	60	21-			6		D	ALIBRATION
_					2		Janua	ary 24, 201
nvir	onm	ent	al	-				
•	Ce	rtifa	cate of		Cal	ibri	ntion	
			Calibration (	Certificatio	n Informat	ion		
Cal. Date:	January 24	2018	Rootsr	neter S/N:	438320	Tav	293	°K
Operator:	Jim Tisch	V1251			450520			1.2.92
		10.20 II 40.30 M				Pa:	756.9	mm Hg
Calibration	Model #:	TE-5025A	Calib	rator S/N:	3166			
		Vol. Init	Vol. Final	ΔVol.	ΔTime	40		1
	Run	(m3)	(m3)			ΔP	ΔH	
	1	1	(113)	(m3) 1	(min) 1.4430	(mm Hg)	(in H2O)	-
	2	3	4	1	1.0270	3.2	2.00	-
	3	5	6	1	0.9220	7.9	5.00	· · ·
	4	7	8	1	0.8780	8.7	5.50	
	5	9	10	1	0.7270	12.6	8.00	
						12.0	0.00	]
			D	ata Tabulat	ion			
	Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right)}$	)( <u>Tstd</u> )		Qa	√∆н(та/Ра)	
	(m3)	(x-axis)	(y-axi	s)	Va	(x-axis)	(y-axis)	
	1.0087	0.6990	1.423	3	0.9958	0.6901	0.8799	
	1.0044	0.9780	2.012		0.9915	0.9655	1.2443	
	1.0024	1.0872	2.250		0.9896	1.0733	1.3912	
	1.0013	1.1404	2.360		0.9885	1.1259	1.4591	-
	0.9961	1.3701	2.846		0.9834	1.3526	1.7598	
	OCTO		2.122			m=	1.32895	
	QSTD	b=	-0.060		QA [	b=	-0.03719	
		r=	0.9999	99		r=	0.99999	
				Calculation	s			1
	Vstd=	ΔVol((Pa-ΔP)	/Pstd)(Tstd/Ta	)	Va=	ΔVol((Pa-ΔF	P)/Pa)	
	Qstd=	Vstd/∆Time			Qa=	Va/∆Time		
			For subseque	ent flow rat	e calculation	IS:		
	Qstd=	1/m (( \\ \ \ \ \ \ \ \ \ \ (	Pa (Tstd Pstd (Ta )	)-b)	Qa=	1/m ((√∆H	(Ta/Pa))-b)	
	Standard	Conditions						La la companya da companya
Tstd:	298.15			Г		RECAL	IBRATION	
Pstd:		nm Hg		H				
		ey					nual recalibratio	
		er reading (in					egulations Part 5	
ΔP: rootsme	ter manome	ter reading (	mm Hg)				Reference Meth	
	Southe temp	erature ("K)			Dotorminati	on of Surn	ended Particulate	Adattar in
Ta: actual ab Pa: actual ba			49)				re, 9.2.17, page 3	Contraction of the second s

Tisch Environmental, Inc. 145 South Miami Avenue



Lam Environmental Services Limited

## Calibration Data for High Volume Sampler (TSP Sampler)

Location	:	CMA1b	Calbration Date :	19-Dec-18
Equipment no.	: _	HVS001	Calbration Due Date :	18-Feb-19

## CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition									
Temperature, T <sub>a</sub>		29	93	Kelvin	Pressure,	Pa	1	020 mmHg	
			Orifice Trans	fer Standard	I Informatic	on			
Equipment No.		Ori31	66	Slope, m <sub>c</sub>	2.122	31	Intercept, bo	<b>c</b> -0.06016	
Last Calibration Date		24-Jan	-18		(HxP	<sub>a</sub> / 1013	3.3 x 298 /	T <sub>a</sub> ) <sup>1/2</sup>	
Next Calibration Date		24-Jan	-19		=	m <sub>c</sub> x	Q <sub>std</sub> + b <sub>c</sub>		
	Calibration of TSP								
Calibration	Ма	nometer	Reading	Q	std	Contin	uous Flow	IC	
Point	н	(inches c	of water)	(m <sup>3</sup> / min.) Record			order, W	W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.3	
	(up)	(down)	(difference)	X-a	xis	(0	CFM)	Y-axis	
1	1.6	1.6	3.2	0.88	312		26	26.3074	
2	2.7	2.7	5.4	1.13	362		34	34.4020	
3	4.0	4.0	8.0	1.37	768		45	45.5321	
4	5.2	5.2	10.4	1.50	658		48	48.5676	
5	6.3	6.3	12.6	1.72	207		54	54.6385	
By Linear Regression of Y c	on X								
S	Slope, m	=	33.7	706	Inte	rcept, b =	-3.	.2329	
Correlation Coe	efficient*	=	0.99	933					
Calibration Accepted =			Yes/	No**	-				

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks	٠
riemans	٠

Calibrated by	:	Henry Lau	Checked by	 Chan Ka Chun
Date	:	19-Dec-18	Date	 19-Dec-18



Lam Environmental Services Limited

# Calibration Data for High Volume Sampler (TSP Sampler)

Location	:	CMA2a	Calbration Date	:	19-Dec-18
Equipment no.	: _	HVS002	Calbration Due Date	:	18-Feb-19

## CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition										
Temperature, T <sub>a</sub>		29	93	Kelvin	Pressure, P <sub>a</sub>			1020	mmHg	
Orifice Transfer Standard Information										
Equipment No.	Ori3166		Slope, m <sub>c</sub>	2.12231		Intercept,	bc	-0.06016		
Last Calibration Date	24-Jan-18		$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$							
Next Calibration Date	24-Jan-19				= $m_c \times Q_{std} + b_c$					
Calibration of TSP										
Calibration	Manometer Reading			Q	std Contin		nuous Flow	IC		
Point	H (inches of water)			(m <sup>3</sup> /	<sup>3</sup> / min.) Reco		order, W	(W(P <sub>a</sub> /10	13.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31)	
	(up)	(down)	(difference)	X-a	axis	(	(CFM)		Y-axis	
1	1.5	1.5	3.0	0.8	541		28		28.3311	
2	2.2	2.2	4.4	1.0	1.0284		32	32.3784		
3	3.7	3.7	7.4	1.3	1.3253		40	40 40.4730		
4	4.5	4.5	9.0	1.4	586		44	44.5203		
5	6.0	6.0	12.0	1.6	799		52		52.6149	
By Linear Regression of Y o	on X									
Slope, m = 29.09		048 Intercept, b = 2.7348								
Correlation Coefficient* =		=	0.99	<del>)</del> 63	_					
Calibration Accepted =		=	Yes/ <del>No</del> **		_					

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Calibrated by	:	Henry Lau	Checked by :	Chan Ka Chun
Date	: _	19-Dec-18	Date :	19-Dec-18



# Calibration Data for High Volume Sampler (TSP Sampler)

Location	:	CMA3a	Calbration Date	:	19-Dec-18
Equipment no.	: _	HVS012	Calbration Due Date	: .	18-Feb-19

#### CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition											
Temperature, T <sub>a</sub>			293	Kelvin	Pressure,	Pa		1020	mmHg		
			Orifice Tr	ransfer Standard	Information	n					
Equipment No.		Ori31	66	Slope, m <sub>c</sub>	2.122	31	Intercept, k	)- oc	0.06016		
Last Calibration Date		24-Jar	า-18		(HxPa	/ 1013.	3 x 298 / T	$(\Gamma_{a})^{1/2}$			
Next Calibration Date		24-Jar	า-19		=	m <sub>c</sub> x	k Q <sub>std</sub> + b	с			
Calibration of TSP											
Calibration	Manometer Reading			Q <sub>std</sub>		Continuous Flow		IC			
Point	H (inches of water)			(m <sup>3</sup> / min.)		Reco	order, W	(W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31			
	(up)	(down)	(difference)	X-axis		(C	CFM)	Y-a	axis		
1	1.2	1.2	2.4	0.7669	)		20	20.2365			
2	2.0	2.0	4.0	0.9819	)		28	28.3311			
3	3.5	3.5	7.0	1.2897	7		37	37.4375			
4	4.5	4.5	9.0	1.4586	;		41	41.4	4848		
5	5.5	5.5	11.0	1.6096	3		50	50.5	5912		
By Linear Regression of Y c	on X										
٤	Slope, m		33	3.7811	Inter	rcept, b =		5.6420	_		
Correlation Coe	efficient*	=	0	).9918	-						
Calibration Accepted =		Ye	Yes/ <del>No</del> **								
					•						

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks :					
Calibrated by	:	Henry Lau	Checked by	:	Chan Ka Chun
Date	: _	19-Dec-18	Date	:	19-Dec-18



# Calibration Data for High Volume Sampler (TSP Sampler)

Location	:	CMA4a	Calbration Date	:	19-Dec-18
Equipment no.	:	HVS004	Calbration Due Date	:	18-Feb-19

#### CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition											
Temperature, T <sub>a</sub>		29	93	Kelvin	Pressure,	Pa		1020	mmHg		
			Orifice Tra	nsfer Stand	ard Informa	ation					
Equipment No.		Ori31	66	Slope, m <sub>c</sub>	2.122	31	Intercept,	bc	-0.06016		
Last Calibration Date		24-Jan	-18		( H x I	P <sub>a</sub> / 101	3.3 x 298	/T <sub>a</sub> )	1/2		
Next Calibration Date		24-Jan	-19		=	m <sub>c</sub> >	۷ Q <sub>std</sub> + b	с			
Calibration of TSP											
Calibration	Manometer Reading			Q	std	Continu	Continuous Flow		IC		
Point	H (inches of water)			(m <sup>3</sup> / min.)		Reco	order, W	$(W(P_a/1013.3x298/T_a)^{1/2}/35.31)$			
	(up)	(down)	(difference)	X-a	xis	(0	CFM)		Y-axis		
1	1.5	1.5	3.0	0.8	541		24		24.2838		
2	2.0	2.0	4.0	0.9	319		31		31.3666		
3	3.6	3.6	7.2	1.3	)76		40		40.4730		
4	4.2	4.2	8.4	1.4	101		47		47.5558		
5	5.7	5.7	11.4	1.6	381		56		56.6622		
By Linear Regression of Y	r on X										
5	Slope, m	=	39.8	624	Inte	rcept, b =	-	9.2955			
Correlation Coefficient* = 0.99			932	_							
Calibration A	ccepted	=	Yes/I	No**	_						

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by	:	Henry Lau	Checked by	Chan Ka Chun
Date	:	19-Dec-18	Date :	19-Dec-18



# Calibration Data for High Volume Sampler (TSP Sampler)

Location	:	CMA5b	Calbration Date	:	19-Dec-18
Equipment no.	:	HVS010	Calbration Due Date	:	18-Feb-19

#### CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition										
Temperature, T <sub>a</sub>		293		Kelvin	Pressure,	Pa		1020	mmHg	
Orifice Transfer Standard Information										
Equipment No.		Ori3166         Slope, mc         2.12231         Intercept, bc         -0							-0.06016	
Last Calibration Date		24-Jan-1	8		( H x F	P <sub>a</sub> / 101	3.3 x 298	/ T <sub>a</sub>	) 1/2	
Next Calibration Date		24-Jan-1	9		=	m <sub>c</sub> >	k Q <sub>std</sub> + b	С		
Calibration of TSP										
Calibration	Manometer Reading			Q	std	Continu	Jous Flow		IC	
Point	H (inches of water)			(m <sup>3</sup> /	min.)	nin.) Recor		(W(P <sub>a</sub> /	/1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31)	
	(up)	(down)	difference	X-a	xis	(0	CFM)		Y-axis	
1	1.5	1.5	3.0	0.85	541		25		25.2956	
2	2.8	2.8	5.6	1.15	566		34		34.4020	
3	3.6	3.6	7.2	1.30	)76		38		38.4493	
4	4.8	4.8	9.6	1.50	)55		46		46.5439	
5	6.0	6.0	12.0	1.67	799		54		54.6385	
By Linear Regression of Y	′ on X									
s	Slope, m	=	35	.1088	Inte	rcept, b =		5.8015	5	
Correlation Coefficient* =			0.	9935						
Calibration A	ccepted	=	Yes	s/ <del>No</del> **						

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by	:	Henry Lau	Checked by :	Chan Ka Chun
Date	:	19-Dec-18	Date :	19-Dec-18



# Calibration Data for High Volume Sampler (TSP Sampler)

Location	:	CMA6a	Calbration Date	:	19-Dec-18
Equipment no.	: _	HVS013	Calbration Due Date	:	18-Feb-19

#### CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition										
Temperature, T <sub>a</sub>		293		Kelvin	Pressure,	ssure, P <sub>a</sub> 1020			mmHg	
Orifice Transfer Standard Information										
Equipment No.		Ori3166	6	Slope, m <sub>c</sub>	2.122	31	Intercept, bc		-0.06016	
Last Calibration Date		24-Jan-1	8		( H x I	P <sub>a</sub> / 10′	13.3 x 298	/ T <sub>a</sub>	) 1/2	
Next Calibration Date		24-Jan-1	9		=	m <sub>c</sub>	x Q <sub>std</sub> + b	с		
Calibration of TSP										
Calibration	Manometer Reading			Q,	std	Contin	uous Flow		IC	
Point	H (inches of water)		(m <sup>3</sup> / min.)		Reco	order, W	$(W(P_a/1013.3x298/T_a)^{1/2}/35.31)$			
	(up)	(down)	difference	X-a	xis	(	CFM)		Y-axis	
1	1.4	1.4	2.8	0.82	261		28		28.3311	
2	2.3	2.3	4.6	1.05	509		33		33.3902	
3	3.7	3.7	7.4	1.32	253		41		41.4848	
4	4.8	4.8	9.6	1.50	)55		46		46.5439	
5	6.0	6.0	12.0	1.67	799		54		54.6385	
By Linear Regression of Y	′ on X									
S	Slope, m	=	30.	.1687	Inte	rcept, b =	- 2	2.3363		
Correlation Coefficient* = 0			0.9	9927						
Calibration A	ccepted	=	Yes	s/ <del>No</del> **						

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by	:	Henry Lau	Checked by :	Chan Ka Chun
Date	:	19-Dec-18	Date :	19-Dec-18



#### 综合試驗 有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website; www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



# CERTIFICATE OF CALIBRATION

Certificate No.:	18CA0322 01		Page	1	of 2	2
Item tested						
Description: Manufacturer: Type/Model No.: Serial/Equipment No.: Adaptors used:	Sound Level Meter ( Larson Davis LxT1 0003737	Type 1)	Microphone PCB 377B02 171529 -			
Item submitted by						
Customer Name: Address of Customer: Request No.: Date of receipt:	Lam Geotechnics Lte - 22-Mar-2018	d.				
Date of test:	28-Mar-2018					
Reference equipment	used in the calibra	tion				
Description: Multi function sound calibrator Signal generator	Model: B&K 4226 DS 360	Serial No. 2288444 61227	Expiry Date: 08-Sep-2018 01-Apr-2018		Traceable ( CIGISMEC CEPREI	to:
Ambient conditions						
Temperature:	21 ± 1 °C					

#### **Test specifications**

Relative humidity:

Air pressure:

- The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of +20%.
- The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

#### **Test results**

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.


Actual Measurement data are documented on worksheets.

Approved Signatory:



50 ± 10 %

1005 ± 5 hPa





Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

Date:

© Soils & Materials Engineering Co. Ltd.

Form No CARP152-1/Issue 1/Rev C/01/02/2007

Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. HOKLAS 028) under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific calibration activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this certificate are traceable to the International System of Units (SI) or recognised measurement standards. This certificate shall not be reproduced except in full.



### 綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD.

· 港 黄 竹 坑 道 3 7 號 利 達 中 心 1 2 樓

12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



2

# CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

18CA0322 01

Page 2 of

#### 1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	
(1) <b>4</b> 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	c	Pass	0.8	2.1
	Lin	Pass	1.6	2.2
Linearity range for Leg	At reference range , Step 5 dB at 4 kHz	Pass	0.3	2.2
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	지수는 모양은 방법에 가지 않는 것 같은 것 같	Pass	0.3	
	AC	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	N/A	N/A	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/10 <sup>3</sup> at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 <sup>4</sup> at 4kHz	Pass	5-20 S	
Pulse range		50.00555	0.3	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

#### 2, Acoustic tests


The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz Weighting A at 8000 Hz	Pass Pass	0.3 0.5	

#### Response to associated sound calibrator

#### N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.



The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

C Soils & Materials Engineering Co. Ltd.

Form No CARP 152-2/lissue 1/Rev C/01/02/2007

Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. HOKLAS 028) under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific calibration activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this certificate are traceable to the International System of Units (SI) or recognised measurement standards. This certificate shall not be reproduced except in full.



#### 综合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香港美行就道 37號利達中心12樓

12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



# CERTIFICATE OF CALIBRATION

Certificate No.:	18CA1114 02			Page	1	of	2
Item tested							
Description:	Sound Level Mete	r (Type 1)	20	Microphone			
Manufacturer:	B&K			B&K			
Type/Model No.:	2236		- 22	4188			
Serial/Equipment No.:	2100736		- 55	2288941			
Adaptors used:	-		- 18 - I	-			
Item submitted by			_				
Customer Name:	Lam Environment	al Service Ltd.					
Address of Customer:		15-50000000000					
Request No .:							
Date of receipt:	14-Nov-2018						
Date of test:	15-Nov-2018						
Reference equipment	used in the calib	ration					
Description:	Model:	Serial No.		Expiry Date:		Traceal	ble to:
Multi function sound calibrator	B&K 4228	2288444		23-Aug-2019		CIGISME	EC
Signal generator	DS 360	33873		24-Apr-2019		CEPREI	
Signal generator	DS 360	61227		23-Apr-2019		CEPREI	
Ambient conditions							
Temperature:	20 ± 1 °C						
Relative humidity:	50 ± 10 %						
Air pressure:	1000 ± 5 hPa						
Test specifications							
1, The Sound Level Met	ter has been calibrati	ed in accordance w	ith the	requirements as sp	ecifie	d in BS 7	580: Part 1
and the lab calibratio	n procedure SMTP00						
	Contraction and the Contraction of the	The second se					

- The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.
- The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

#### Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Approved Signatory: Date: 15-Nov-2018 Company Chop:

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-18 num 1/Rev.C/01/02/2007

Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. HOKLAS 928) under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific calibration activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this certificate are traceable to the International System of Units (SI) or recognised measurement standards. This certificate shall not be reproduced except in full.



### 綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD.

香 憲 黄 竹 坑 道 3 7 號 利 嶠 中 心 1 2 樓 12F., Laader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



2

## CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

18CA1114 02

Page

of

#### **Electrical Tests** 1.

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	
	C	Pass	1.0	2.1
	Lin	Pass	2.0	2.2
Linearity range for Leg	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	A	Pass	0.3	
the desired stars we get	C	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
15 BAD OF #1000#154	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	Pass	0.3	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
Contraction and an end of the second	Repeated at frequency of 100 Hz	Pass.	0.3	
Time averaging	1 ms burst duty factor 1/10 <sup>3</sup> at 4kHz	Pass	0.3	
00.014-012000000000000000000000000000000000	1 ms burst duty factor 1/10 <sup>4</sup> at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
5 1 1 1 1 M M M M M M M M M M M M M M M	Lea	Pass	0.4	

#### 2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
6648877.0003978787891495	Weighting A at 8000 Hz	Pass	0.5	

#### Response to associated sound calibrator 3.

#### N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

	1	- End -	Amin	
Calibrated by:	~ 7	Checked by:	- 1-44	
Date:	Fung Chi Yip 15-Nov-2018	Date:	/Shek Kwong Tat 15-Nov-2018	

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Sote & Materials Engineering Co., UM

Form No CARP152-2/Issue 1/Rev C/01/02/2007

Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. HOKLAS 028) under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific calibration activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this certificate are traceable to the International System of Units (SI) or recognised measurement standards. This certificate shall not be reproduced except in full,



# 綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香 徳 黄 竹 坑 砲 3 7 號 利 達 中 心 1 2 樓 12F., Loader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong,

E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533

24-Apr-2019



# CERTIFICATE OF CALIBRATION

Certificate No.:	18CA1220 02		Page:	1 of 2
Item tested				
Description:	Acoustical Calib	ator (Class 1)		
Manufacturer:	Larson Davis	2010/07/07/07/07		
Type/Model No.:	CAL200			
Serial/Equipment No.:	13128			
Adaptors used:	(0.259350) 55			
Item submitted by				
Curstomer:	Lam Environmer	tal Service Ltd.		
Address of Customer:				
Request No.:	ini Marananana			
Date of receipt:	20-Dec-2018			
Date of test:	28-Dec-2018			
Reference equipment	used in the cali	bration		
Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2412857	20-Apr-2019	SCL
Preamplifier	B&K 2673	2239857	27-Apr-2019	CEPREI
Measuring amplifier	B&K 2610	2346941	08-May-2019	CEPREI
Signal generator	DS 360	33873	24-Apr-2019	CEPREI
Digital multi-meter	34401A	US36087050	23-Apr-2019	CEPREI
Audio analyzer	89038	GB41300350	23-Apr-2019	CEPREI

#### Ambient conditions

Universal counter

Temperature:	20 ± 1 °C
Relative humidity:	50 ± 10 %
Air pressure:	1000 ± 5 hPa

53132A

#### Test specifications

1. The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.

MY40003662

- 2. The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- З, The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference. pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.


#### Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942, 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.

al

Fend



Jungi

29-Dec-2018 Company Chop:



Comments: The results reported in this certificate refer to the conditon of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

Date:

© Soits & Material's Engineering Coll Ltd.

Farm No. CARP106-54ssue 1/Rev. Dt01/03/2007

CEPREI

Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. HOKLAS 028) under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific calibration activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this certificate are traceable to the International System of Units (SI) or recognised measurement standards. This certificate shall not be reproduced except in full.



### 綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD.

香 進 黄 竹 坑 道 3 7 號 利 達 中 心 1 2 樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



## CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

18CA1220 02

2 Page:

#### Measured Sound Pressure Level 1.

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

Frequency	Output Sound Pressure	Measured Output	Estimated Expanded
Shown	Level Setting	Sound Pressure Level	Uncertainty
Hz	dB	d8	dB
1000	94.00	93.84	0.10

#### 2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz	STF = 0.006 dB

Estimated expanded uncertainty

#### 3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

0.005 dB

At 1000 Hz	Actual Frequency = 999.4 Hz		
Estimated expanded uncertainty	0.1 Hz	Coverage factor k = 2:2	

#### 4, **Total Noise and Distortion**

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was

At 1000 Hz	TND = 0.4%
Estimated expanded uncertainty	0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

	Λ	- End -	1
Calibrated by:	$1 - \chi$	Checked by:	Aque
Date:	28-Dec-2018	Date:	Shek Kwong Tat 29-Dec-2018

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

ID Solis & Materials Engineering Co., Ltd.

Form No.CARP198-24soue 1/Rev.CI01/05/2005

Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. HOKLAS 028) under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific calibration activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this certificate are traceable to the International System of Units (SI) or recognised measurement standards. This certificate shall not be reproduced except in full.



#### EQUIPMENT PERFORMANCE CHECK / CALIBRATION REPORT

Report No.	: HK1811027
Project Name	EQUIPMENT PERFORMANCE CHECK/CALIBRATION REPORT
Date of Issue	: 11/10/2018
Customer	LAM ENVIRONMENTAL SERVICES LIMITED
Address	: 11/F., CENTRE POINT, 181-185 GLOUCESTER ROAD, WAN CHAI, HONG KONG
Calibration Job No.	HK1811027
Test Item No.	HK1811027-01
Test Item Details	
Test Item Description	: Sonde
Manufacturer	: YSI
Model No.	Professional Plus
Serial No.	: 14M100277
Performance Method	Checked according to in-house method CAL005
	(References: Temperature (Section 6 of Intermational Accreditation New Zealand Technical G
	No. 3 Second edition March 2008: Working Thermometer Calibration Procedure), pH value
	(APHA 21e 4500H:B), Salinity (Refer to Conductivity APHA 19e 2510B)
	, Dissolved oxygen (APHA 19e 4500-O.C))
Test Item Receipt Date	: 11/10/2018
<b>Test Item Calibration Date</b>	: 11/10/2018

Notes: 1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.

- 2. Results relate to item(s) as received.
- 3. ± indicates the tolerance limit
- 4. N/A = Not applicable
- 5. APHA American Public Health Association, American Water Works Association and Water Environment Federation, Standard Methods for the Examination of Water and Wastewater, APHA-AWWA-WEF, USA
- 6. DO, pH, salinity and temperature performance check was conducted by Pilot Testing Limited.
- Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

Approved Signatory

Issue Date:

11/10/2018

Ms. Wong Po Yan, Pauline (Assistant Laboratory Manager)



#### REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

#### WORK ORDER: HK1811027 DATE OF ISSUE: 11/10/2018 CLIENT: LAM ENVIRONMENTAL SERVICES LIMITED

Equipment Type	Sonde	
Manufacturer	YSI	
Model No.	Professional Plus	
Serial No.	14M100277	
Date of Calibration	11-Oct-18	
Date of next Calibation	11-Jan-19	

#### Parameters:

#### Temperature (Method Ref: Section 6 of Intermational Accreditation New Zealand Technical Guide No.3 Second edition March 2008: Working Thermometer Calibration Procedure)

Reference Reading (*C)	Display Reading (°C)	Deviation (°C)
7.0	6.9	-0.1
15.7	16.0	0.4
24.7	24.5	-0.2
T	olerance Limit	±2.0

#### pH Value (Method Ref: APHA21e, 4500H:B)

Expected Reading (pH unit)	Reference Reading (pH unit)	Display Reading (pH unit)	Deviation (pH unit)
4.0	3.99	3.98	-0.01
7.0	7.01	7.08	0.07
10.0	10.02	10.06	0.04
	Tolerance Limit		±0.20

#### Conductivity (Method Ref: APHA 19e, 2510)

KCI concentration (mol/L)	Reference Reading (ms/cm)	Display Reading (ms/cm)	Deviation (%)
0.0000	0.00	0.00	
0.1000	12.6	12.6	-0.55
0.2000	23.6	23.6	-0.08
0.5000	55.1	55.7	1.09
	Tolerance Limit		±2.0

#### Dissolved Oxygen (DO) (Method Ref: APHA 19e, 4500-O, C)

Reference DO reading (mg/L)	DO reading od DO probe (mg/L)	Deviation (mg/L)
6.97	6.92	-0.05
5.15	5.10	-0.05
3.97	4.08	0.11
	Tolerance Limit	±0.20

Remarks:

(1) Maxium tolerance and calibration frequency stated in the report, unless otherewise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

(2) Displayed reading presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

(3) Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

- End of Report -



ALS Technichem (HK) Pty Ltd 11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street, Kwai Chung N.I., Hong Kong T: +852 2610 1044 | F: +852 2610 2021

# **REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION**

CONTACT: MR CHAN KA CHUN

CLIENT: LAM ENVIRONMENTAL LTD

ADDRESS: 11/F, CENTRE POINT, 181 - 185 GLOUCESTER ROAD WAN CHAI, HONG KONG WORK ORDER: HK19

HK1900006

SUB-BATCH: 0 LABORATORY: HONG KONG DATE RECEIVED: 31- Dec- 2018 DATE OF ISSUE: 10- Jan- 2019

## COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the ALS Hong Kong laboratory or guoted from relevant international standards.

 Scope of Test:
 Dissolved Oxygen, pH Value, Salinity and Temperature

 Equipment Type:
 Multifunctional Meter

 Brand Name:
 YSI

 Model No.:
 Professional Plus

 Serial No.:
 14M100277

 Equipment No.:
 - 

 Date of Calibration:
 10 January, 2019

NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

no An

Mr Chan Siu Ming, Vico Manager - Inorganic

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

WORK	ORDER:	HK1900006

SUB-BATCH:	0
DATE OF ISSUE:	10- Jan- 2019
CLIENT:	LAM ENVIRONMENTAL LTD
Equipment Type:	Multifunctional Meter
Brand Name:	YSI
Model No.:	Professional Plus
Carlal Ma .	144100277

Serial No.: Equipment No.: Date of Calibration:

14M100277 10 January, 2019

Date of Next Calibration: 10 April, 2019

## PARAMETERS: **Dissolved** Oxygen

Method Ref: APHA (21st edition), 4500-O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
2.67	2.47	- 0.20
6.20	6.28	+0.08
8.88	8.83	- 0.05
	Tolerance Limit (mg/L)	±0.20

pH Value

Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)
4.0	3.97	- 0.03
7.0	6.84	- 0.16
10.0	10.03	+ 0.03
12 (25)34.)	Tolerance Limit (pH unit)	±0.20

Salinity

### Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	
10	10.36	+3.6
20	18.90	- 5.5
30	27.77	- 7.4
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Cha Ain

Mr Chan Siu Ming, Vico Manager - Inorganic

# **REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION**

WORK ORDER:	HK1900006			ALS
SUB-BATCH:	0			(,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,
DATE OF ISSUE:	10- Jan- 2019			
CLIENT:	LAM ENVIRONMENTAL LTD			
Equipment Type:	Multifunctional Meter			
Brand Name:	YSI			
Model No.:	Professional Plus			
Serial No.:	14M100277			
Equipment No.:	terrer i terrer			
Date of Calibration:	10 January, 2019	Date of Next Calibration:	10 April, 2019	

## PARAMETERS: Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
10.5	11.3	+ 0.8
21.0	19.8	- 1.2
40.5	39.4	- 1.1
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ma Ain

A

Mr Chan Siu Ming, Vico Manager - Inorganic



#### EQUIPMENT PERFORMANCE CHECK / CALIBRATION REPORT

Report No. Project Name Date of Issue	HK1811013 EQUIPMENT PERFORMANCE CHECK/CALIBRATION REPORT 10/10/2018
Customer	LAM ENVIRONMENTAL SERVICES LIMITED
Address	11/F., CENTRE POINT, 181-185 GLOUCESTER ROAD, WAN CHAI, HONG KONG
Calibration Job No.	HK1811013
Test Item No.	HK1811013-01
Test Item Details	
Test Item Description	Sonde
Manufacturer	YSI
Model No.	Professional Plus
Serial No.	17F100236
Performance Method	Checked according to in-house method CAL005
	(References: Temperature (Section 6 of International Accreditation New Zealand Technical G
	No. 3 Second edition March 2008: Working Thermometer Calibration Procedure), pH value
	(APHA 21e 4500H:B), Salinity (Refer to Conductivity APHA 19e 2510B.)
	Dissolved oxygen (APHA 19e 4500-O.C))
Test Item Receipt Date	8/10/2018
Test Item Calibration Date	9/10/2018

Notes : 1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.

- 2. Results relate to item(s) as received.
- 3. ± indicates the tolerance limit
- 4. N/A = Not applicable
- 5. APHA American Public Health Association, American Water Works Association and Water Environment Federation, Standard Methods for the Examination of Water and Wastewater, APHA-AWWA-WEF, USA
- DO, pH, salinity and temperature performance check was conducted by Pilot Testing Limited.
   Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

Approved Signatory

Ms. Wong Po Yan, Pauline

(Assistant Laboratory Manager)

Issue Date:

10/10/2018



#### REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

#### WORK ORDER: HK1811013 DATE OF ISSUE: 10/10/2018 CLIENT: LAM ENVIRONMENTAL SERVICES LIMITED

Equipment Type	Sonde	
Manufacturer	YSI	
Model No.	Professional Plus	
Serial No.	17F100236	
Date of Calibration	09-Oct-18	
Date of next Calibation	09-Jan-19	

#### Parameters:

#### Temperature (Method Ref: Section 6 of Intermational Accreditation New Zealand Technical Guide No.3 Second edition March 2008: Working Thermometer Calibration Procedure)

Reference Reading ("C)	Display Reading (°C)	Deviation (°C)
6.3	6.3	0.0
14.6	14.4	-0.2
25.6	25.5	-0.1
Т	olerance Limit	±2.0

#### pH Value (Method Ref: APHA21e, 4500H:B)

Expected Reading (pH unit)	Reference Reading (pH unit)	Display Reading (pH unit)	Deviation (pH unit)
4.0	3.99	4.01	0.02
7.0	6.97	7.01	0.04
10.0	10.03	10.04	0.01
	Tolerance Limit		±0.20

#### Conductivity (Method Ref: APHA 19e, 2510)

KCI concentration (mol/L)	Reference Reading (ms/cm)	Display Reading (ms/cm)	Deviation (%)
0.0000	0.00	0.00	
0.1000	12.2	12.1	-0.33
0.2000	24.0	23.9	-0.58
0.5000	57.1	56.9	-0.32
	Tolerance Limit		±2.0

#### Dissolved Oxygen (DO) (Method Ref: APHA 19e, 4500-O, C)

Reference DO reading (mg/L)	DO reading od DO probe (mg/L)	Deviation (mg/L)
7.14	7.18	0.04
6.79	6.81	0.02
4.80	4.93	0.13
	Tolerance Limit	±0.20

Remarks:

(1) Maxium tolerance and calibration frequency stated in the report, unless otherewise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

(2) Displayed reading presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

(3) Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

- End of Report -



ALS Technichem (HK) Pty Ltd 11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street, Kwai Chung N.T., Hong Kong T: +852 2610 1044 | F: +852 2610 2021

# **REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION**

CONTACT:	MR CHAN KA CHUN	WORK ORDER:	HK1901812
CLIENT:	LAM ENVIRONMENTAL LTD		
ADDRESS:	11/F, CENTRE POINT,	SUB-BATCH:	0
	181 - 185 GLOUCESTER ROAD	LABORATORY:	HONG KONG
	WAN CHAI	DATE RECEIVED:	10-Jan-2019
		DATE OF ISSUE:	18-Jan-2019

# <u>COMMENTS</u>

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.

Scope of Test:	Dissolved Oxygen, pH Value, Salinity and Temperature
Equipment Type:	Multifunctional Meter
Brand Name:	YSI
Model No.:	Professional Plus
Serial No .:	17F100236
Equipment No.:	
Date of Calibration:	18 January, 2019

## <u>NOTES</u>

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Cha Si

Mr Chan Siu Ming, Vico Manager - Inorganic

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

# **REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION**

ALS

WORK ORDER: HK1901812

SUB-BATCH:	0
DATE OF ISSUE:	18-Jan-2019
CLIENT:	LAM ENVIRONMENTAL LTD
Equipment Type:	Multifunctional Meter

Equipment Type:	Multifunctional Meter	
Brand Name:	YSI	
Model No.:	Professional Plus	
Serial No.:	17F100236	
Equipment No.:		
Date of Calibration:	18 January, 2019	Da

Date of Next Calibration:

18 April, 2019

## PARAMETERS:

#### Dissolved Oxygen Method Ref: APHA (21st edition), 4500- O: G

Expected Reading (mg/ L)	Displayed Reading (mg/ L)	Tolerance (mg/ L)
2.65	2.45	- 0.20
6.02	5.92	- 0.10
8.88	8.94	+ 0.06
	Tolerance Limit (mg/L)	±0.20

pH Value

## Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)	
4.0	4.03	+ 0.03	
7.0	7.08	+ 0.08	
10.0	10.16	+0.16	
	Tolerance Limit (pH unit)	±0.20	

#### Salinity

#### Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	
10	10.20	+ 2.0
20	19.68	- 1.6
30	29.74	- 0.9
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ma Ain

Mr Chan Siu Ming, Vico Manager - Inorganic

# **REPORT OF EQUIPMENT PERFORMANCE CHECK/ CALIBRATION**

WORK ORDER:	HK1901812			S
SUB-BATCH: DATE OF ISSUE: CLIENT:	0 18-Jan-2019 LAM ENVIRONMENTAL LTD			
Equipment Type: Brand Name: Model No.: Serial No.: Equipment No.: Date of Calibration:	Multifunctional Meter YSI Professional Plus 17F100236  18 January, 2019	Date of Next Calibration:	18 April, 2019	

## PARAMETERS: Temperature

## Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
10.0	9.5	- 0.5
22.0	21.3	- 0.7
41.5	42.3	+ 0.8
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Cha Aiz

Mr Chan Siu Ming, Vico Manager - Inorganic

Page 1/2



#### REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Information suppli	ed by customer:	
CONTACT:	MR. SAM LAM	WORK ORDER: HK1811070
CLIENT:	LAM GEOTECHNICS I	IMITED
DATE RECEIVED	: 24/10/2018	
DATE OF ISSUE:	25/10/2018	
ADDRESS:	11/F, CENTRE POINT, 1	81-185, GLOUCESTER ROAD,
	WANCHAI, HONG KO?	NG
PROJECT:		

#### METHOD OF PERFORMANCE CHECK/ CALIBRATION: Ref: APHA22nd ed 2130B

## COMMENTS

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

Turbidity	
Turbidimeter	
Xin Rui	
WGZ-3B	
1309192	
25/10/2018	
	Turbidimeter Xin Rui WGZ-3B 1309192 

Remarks:

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Approved Signatory:

Ms. Wong Po Yan, Pauline Assistant Laboratory Manager Issue Date:

25/10/2018





#### REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

#### WORK ORDER: HK1811070 DATE OF ISSUE: 25/10/2018

CLIENT: LAM GEOTECHNICS LIMITED

Equipment Type:	Turbidimeter	
Brand Name:	Xin Rui	
Model No.:	WGZ-3B	
Serial No.:	1309192	
Equipment No.:		
Date of Calibration:	25/10/2018	
Date of next Calibation:	25/01/2019	

#### Parameters:

Turbidity

Method Ref: APHA 22nd ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance	
0	0.00		
4	3.95	-1.3%	
10	10.58	5.8%	
40	39.06	-2.3%	
100	100.50	0.5%	
400	397	-0.7%	
1000	997	-0.3%	
2-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1-1	Tolerance Limit (±)	10%	

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

1/2 Page



#### REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Information supplied	by customer:		
CONTACT:	MR. SAM LAM	WORK ORDER:	HK1811147
CLIENT:	LAM GEOTECHNICS LIMITED		
DATE RECEIVED:	16/11/2018		
DATE OF ISSUE:	19/11/2018		
ADDRESS:	11/F, CENTRE POINT, 181-185, G	LOUCESTER ROAL	D,
	WANCHAI, HONG KONG		
PROJECT:	and the second		

#### METHOD OF PERFORMANCE CHECK/ CALIBRATION: Ref: APHA22nd ed 2130B

#### COMMENTS

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

Scope of Test:	Turbidity	
Equipment Type:	Turbidimeter	
Brand Name:	Xin Rui	
Model No.:	WGZ-3B	
Serial No.:	1403009	
Equipment No.:	200	
Date of Calibration:	19/11/2018	

#### Remarks:

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Approved Signatory:

Ms. Wong Po Yan, Pauline Assistant Laboratory Manager

Issue Date:

19/11/2018

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

Address: No.B12, 5th Floor, Block B, Tonic Industrial Centre, No.19 Lam Hing Street, Kowloon Bay, Kowloon Phone +852 2527 6691 | Email info@pilot-testing.com

PILOT

## REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

WORK ORDER:	HK1811147
DATE OF ISSUE:	19/11/2018
CLIENT:	LAM GEOTECHNICS LIMITED

Equipment Type:	Turbidimeter		
Brand Name:	Xin Rui		
Model No.:	WGZ-3B		
Serial No.:	1403009		
Equipment No.:	444		
Date of Calibration:	19/11/2018		
Date of next Calibation:	19/02/2019		

## Parameters:

Turbidity

Method Ref: APHA 22nd ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance	
0	0.00		
4	3.98	-0.5%	
10	10.12	1.2%	
40	43.50	8.8%	
100	103.00	3.0%	
400	396	-1.0%	
1000	925	-7.5%	
	Tolerance Limit (±)	10%	

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.



#### **REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

Information supplies	d by customer:	
CONTACT:	MR. SAM LAM	WORK ORDER: HK1811031
CLIENT:	LAM GEOTECHNICS I	IMITED
DATE RECEIVED:	11/10/2018	
DATE OF ISSUE:	12/10/2018	
ADDRESS:	11/F, CENTRE POINT,	181-185, GLOUCESTER ROAD,
	WANCHAI, HONG KO	NG
PROJECT:		

#### METHOD OF PERFORMANCE CHECK/ CALIBRATION: Ref: APHA22nd ed 2130B

**COMMENTS** 

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

Scope of Test:	Turbidity		
Equipment Type:	Turbidity Meter		
Brand Name:	PCE Instruments		
Model No.:	PCE-TUM 20		
Serial No.:	0942542		
Equipment No.:			
Date of Calibration:	12/10/2018		

Remarks:

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Approved Signatory:

Ms. Wong Po Yan, Pauline Assistant Laboratory Manager Issue Date:

12/10/2018



### REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

WORK ORDER:	HK1811031
DATE OF ISSUE:	12/10/2018
CLIENT:	LAM GEOTECHNICS LIMITED

Equipment Type:	Turbidity Meter	
Brand Name:	PCE Instruments	
Model No.:	PCE-TUM 20	
Serial No.:	Q942542	
Equipment No.:		
Date of Calibration:	12/10/2018	
Date of next Calibation:	12/01/2019	

#### Parameters:

Turbidity

Method Ref: APHA 22nd ed. 2130B

Expected Reading (NTU)	pected Reading (NTU) Display Reading (NTU)		
0	0.00	***	
10	10.50	5.0%	
20	20.50	2.5%	
40	41.48	3.7%	
100	99	-1.0%	
400	401	0.3%	
800	788	-1.5%	
	Tolerance Limit (±)	10%	

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.



Appendix 5.1

Monitoring Schedules for Reporting Month and Coming Reporting Month

#### Contract No. HK/2015/01

#### Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3) Environmental Monitoring Schedule January 2019

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				27-Dec	28-Dec	29-Dec
				24hr TSP Noise (daytime) (M1a, M4b, M5b,	1hr TSP	
				M6)		
				Impact WQM		Impact WQM
				Mid-ebb 3:29		Mid-ebb 5:24
				Mid-flood 10:41		Mid-flood 12:29
30-Dec	31-Dec	1-Jan	2-Jan	3-Jan	4-Jan	5-Jan
			24hr TSP	1hr TSP		
			Noise (daytime) (M4b, M5b, M6)		Noise (daytime) (M1a)	
	Impact WQM		Impact WQM		Impact WQM	
	Mid-ebb 7:43		Mid-flood 11:47		Mid-flood 16:48	
	Mid-flood 14:13		Mid-ebb 22:38		Mid-ebb 23:50	
6-Jan	7-Jan	8-Jan	9-Jan	10-Jan	11-Jan	12-Jan
		24hr TSP	1hr TSP			
		Noise (daytime) (M1a, M4b, M5b,	-			
		M6)				
	Impact WQM		Impact WQM		Impact WQM	
	Mid-ebb 0:57		Mid-ebb 1:58		Mid-ebb 2:53	
	Mid-flood 8:12		Mid-flood 9:19		Mid-flood 10:30	
13-Jan	14-Jan	15-Jan	16-Jan	17-Jan	18-Jan	19-Jan
	24hr TSP (CMA1b, CMA3a,	Other TOD (OMAGE)			24hr TSP (CMA1b, CMA2a,	04h- TOD (OMA 4-)
	CMA4a, CMA5b, CMA6a)	24hr TSP (CMA2a) 1hr TSP			CMA3a, CMA5b, CMA6a)	24hr TSP (CMA4a) 1hr TSP
	Noise (daytime) (M1a,)	nii toi.		Noise (daytime) (M4b, M5b)	Noise (daytime) (M6)	mi tor
	Impact WQM		Impact WQM		Impact WQM	
	Mid-ebb 4:44		Mid-flood 13:50		Mid-flood 15:19	
	Mid-flood 12:30		Mid-lobd 13:30 Mid-ebb 21:00		Mid-toba 13:13 Mid-ebb 22:34	
20-Jan	21-Jan	22-Jan	23-Jan	24-Jan	25-Jan	26-Jan
			24hr TSP	1hr TSP		
		Noise (daytime) (M4b, M5b)			Noise (daytime) (M1a, M6)	
	Impact WQM		Impact WQM		Impact WQM	
	Mid-ebb 0:05		Mid-ebb 1:40		Mid-flood 10:04	
	Mid-flood 7:07		Mid-flood 8:36	1	Mid-ebb 15:44	

Remark:

Due to interruption of electricity, the 24hr TSP at CMA2a was rescheduled from 14 January 2019 to 15 January 2019. Due to interruption of electricity, the 24hr TSP at CMA4a was rescheduled from 18 January 2019 to 19 January 2019.

#### Contract No. HK/2015/01 Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3) Tentative Environmental Monitoring Schedule February 2019

Sunday	Monday		Tuesday	Wednesday		Thursday	Friday	Saturday
27-J	n	28-Jan	29-Jar	1	30-Jan	31-Jan	1-Feb	2-Feb
	24hr TSP		1hr TSP				24hr TSP	1hr TSP
	Noise (daytime)		Noise (daytime)				2411 105	ini i ar
	Impact WQM Mid-flood	12:23		Impact WQM Mid-flood	14:03		Impact WQM Mid-flood 15:41	
	Mid-ebb	19:03		Mid-ebb	22:02		Mid-ebb 23:05	
3-Fe	b	4-Feb	5-Fet	>	6-Feb	7-Feb	8-Feb	9-Feb
	24hr TSP Noise (daytime)						1hr TSP Noise (daytime)	
	Impact WQM			Impact WQM			Impact WQM	
	Mid-ebb	0:08		Mid-ebb	1:10		Mid-ebb 2:08	
	Mid-flood	7:19		Mid-flood	8:13		Mid-flood 9:00	10.5.1
10-Fe	0	11-Feb	12-Feb		13-Feb	14-Feb	15-Feb	16-Feb
				24hr TSP		1hr TSP		
	Noise (daytime)		Noise (daytime)	24111 1 3F		nii tor		
	Impact WQM			Impact WQM			Impact WQM	
	Mid-flood	10:36		Mid-flood	11:56		Mid-flood 13:35	
17-Fr	Mid-ebb	16:49 18-Feb	19-Feb	Mid-ebb	19:05 20-Feb	21-Feb	Mid-ebb 21:19 22-Feb	23-Feb
		10100	10102		20100	21100	EL 100	20100
	Į							
	I							
			24hr TSP	1hr TSP				
	Noise (daytime)		Noise (daytime)					
	Impact WQM			Impact WQM			Impact WQM	
	Mid-flood	16:53		Mid-ebb	13:03		Mid-flood 8:38	
24-Fr	Mid-ebb	23:52 25-Feb	26-Feb	Mid-flood	18:43		Mid-ebb 14:27	
				1				
				1				
	24hr TSP		1hr TSP					
	Noise (daytime)		Noise (daytime)	1				
				1				
	Impact WQM			1				
	Mid-flood	10:31		1				
	Mid₊ebb	16:50						



Appendix 5.2

Noise Monitoring Results and Graphical Presentations



#### Noise Monitoring Result

#### Day Time (0700 - 1900hrs on normal weekdays)

Location: M1a - Footbridge at EX-Wanchai Harbour Road Sports Centre

			Measurement Noise Level Baseline Level Construction Noise Level Limit Level							Measurement Noise Level			Limit Level
Date	Time	Weather	Leq	L10	L90	Leq	Leq	Leq					
			Unit: dB(A), (30-min)										
27/12/18	16:55	Cloudy	71.8	73.7	69.4	72	72	75					
4/1/18	13:00	Cloudy	74.7	77.4	71.7	72	71	75					
8/1/19	16:45	Cloudy	72.2	74.5	68.3	72	72	75					
14/1/19	13:00	Cloudy	72.1	74.0	68.5	72	72	75					
25/1/19	13:05	Fine	74.3	77.0	73.0	72	70	75					



Noise Monitoring Result

#### Day Time (0700 - 1900hrs on normal weekdays)

Location: M4b - Victoria Centre

		Measure	ment Noise Level Baseline Noise Level Construction Noise Level Limit Level					
Date	Time	Weather	Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30min)					
27/12/18	8:35	Cloudy	66.2	67.0	63.3	67	66	75
2/1/18	08:40	Cloudy	66.2	67.6	63.1	67	66	75
8/1/19	10:35	Cloudy	71.9	74.7	65.0	67	70	75
17/1/19	08:37	Fine	66.7	68.0	62.0	67	67	75
22/1/19	14:55	Fine	70.0	71.0	63.5	67	67	75

Location: M5b - City Garden


			Measure	ement Noi	se Level	Baseline Level	Construction Noise Level	Limit Level						
Date Time		me Weather		L10	L90	Leq	Leq	Leq						
				Unit: dB(A), (30min)										
27/12/18	10:00	Cloudy	69.1	70.4	67.4	68	63	75						
2/1/19	10:35	Cloudy	70.3	72.5	69.2	68	66	75						
8/1/19	09:00	Cloudy	70.5	73.0	67.3	68	67	75						
17/1/19	10:05	Fine	69.4	71.7	67.3	68	64	75						
22/1/19	16:05	Fine	74.9	76.0	71.0	68	74	75						


Location: M6 - HK Baptist Church Henrietta Secondary School


			Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level						
Date Time		Time Weather		Leg L10 L90 Leg Leg		Leq	Leq							
				Unit: dB(A), (30-min)										
27/12/18	10:37	Cloudy	69.3	69.3 70.7 67.4		71	69	70						
2/1/19	11:10	Cloudy	68.7	69.6	67.3	71	69	70						
8/1/19	9:38	Cloudy	67.2	68.7	65.1	71	67	70						
18/1/19	10:50	Fine	67.8	69.0	66.0	71	68	65						
25/1/19	11:20	Fine	68.9	69.5	67.0	71	69	65						




Graphic Presentation of Noise Monitoring Result Day Time (0700 - 1900hrs on normal weekdays)











Appendix 5.3

Air Quality Monitoring Results and Graphical Presentations

Location: CMA1b - Harbour Grand Hotel Boundary Wall

### Report on 24-hour TSP monitoring

Action Level (  $\mu\,\text{g/m3}\text{)}$  - 176.7

Limit Level ( µ g/m3) - 260

Date	Sampling	Weather	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling	mpling Flow		min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, $Q_{si}$	Final, $Q_{sf}$	Average	Volume, m <sup>3</sup>	μg/m <sup>3</sup>
27-Dec-18	8:00	Cloudy	CMA1b_24hr 140128	2.6539	2.7333	12929.16	12953.16	24.00	1.19	1.19	1.19	1712	46.4
2-Jan-19	8:00	Cloudy	CMA1b_24hr 140181	2.6527	2.7330	12956.16	12980.16	24.00	1.20	1.20	1.20	1728	46.5
8-Jan-19	8:00	Fine	CMA1b_24hr 140166	2.6421	2.7679	12983.16	13007.16	24.00	1.19	1.19	1.19	1716	73.3
14-Jan-19	8:00	Cloudy	CMA1b_24hr 140241	2.6737	2.7664	13010.17	13034.17	24.00	1.19	1.19	1.19	1713	54.1
18-Jan-19	8:00	Fine	CMA1b_24hr 140241	2.6781	2.7825	13037.17	13061.17	24.00	1.19	1.19	1.19	1717	60.8
23-Jan-19	8:00	Fine	CMA1b_24hr 140385	2.6554	2.7976	13064.17	13088.17	24.00	1.20	1.19	1.19	1721	82.6

#### Report on 1-hour TSP monitoring Action Level (µg/m3) - 320.1 Limit Level (µg/m3) - 500

Date	Sampling	Weather	Filter paper no.	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flow Rate, m <sup>3</sup> /min		min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, $Q_{si}$	Final, $Q_{sf}$	Average	Volume, m <sup>3</sup>	μg/m <sup>3</sup>
28-Dec-18	8:09	Cloudy	CMA1b_1hr_1 140010	2.6817	2.6852	12953.16	12954.16	1.00	1.19	1.19	1.19	72	48.9
28-Dec-18	9:12	Cloudy	CMA1b_1hr_2 140012	2.6843	2.6893	12954.16	12955.16	1.00	1.19	1.19	1.19	72	69.8
28-Dec-18	10:15	Cloudy	CMA1b_1hr_3 140015	2.6606	2.6674	12955.16	12956.16	1.00	1.19	1.19	1.19	72	95.0
3-Jan-19	8:03	Cloudy	CMA1b_1hr_1 140187	2.6478	2.6523	12980.16	12981.16	1.00	1.20	1.20	1.20	72	62.6
3-Jan-19	10:27	Cloudy	CMA1b_1hr_2 206799	2.6812	2.6828	12981.16	12982.16	1.00	1.20	1.20	1.20	72	22.3
3-Jan-19	13:00	Cloudy	CMA1b_1hr_3 206764	2.6867	2.6889	12982.16	12983.16	1.00	1.20	1.20	1.20	72	30.6
9-Jan-19	9:30	Fine	CMA1b_1hr_1 140216	2.6643	2.6702	13007.17	13008.17	1.00	1.19	1.19	1.19	72	82.4
9-Jan-19	10:58	Fine	CMA1b_1hr_2 140227	2.6677	2.6728	13008.17	13009.17	1.00	1.19	1.19	1.19	72	71.2
9-Jan-19	13:00	Fine	CMA1b_1hr_3 140234	2.6774	2.6835	13009.17	13010.17	1.00	1.19	1.19	1.19	72	85.2
15-Jan-19	8:25	Cloudy	CMA1b_1hr_1 140259	2.6759	2.6801	13034.17	13035.17	1.00	1.19	1.19	1.19	71	58.8
15-Jan-19	9:55	Cloudy	CMA1b_1hr_2 140265	2.6814	2.6854	13035.17	13036.17	1.00	1.19	1.19	1.19	71	56.0
15-Jan-19	10:58	Cloudy	CMA1b_1hr_3 140274	2.6573	2.6607	13036.17	13037.17	1.00	1.19	1.19	1.19	71	47.6
19-Jan-19	8:02	Fine	CMA1b_1hr_1 140259	2.6725	2.6804	13061.17	13062.17	1.00	1.19	1.19	1.19	71	110.6
19-Jan-19	9:55	Fine	CMA1b_1hr_2 140265	2.6684	2.6803	13062.17	13063.17	1.00	1.19	1.19	1.19	71	166.6
19-Jan-19	13:00	Fine	CMA1b_1hr_3 140274	2.6606	2.6652	13063.17	13064.17	1.00	1.19	1.19	1.19	71	64.4
24-Jan-19	8:55	Fine	CMA1b_1hr_1 140318	2.6734	2.6811	13088.17	13089.17	1.00	1.19	1.19	1.19	72	107.5
24-Jan-19	10:58	Fine	CMA1b_1hr_2 140329	2.6628	2.6688	13089.17	13090.17	1.00	1.19	1.19	1.19	72	83.8
24-Jan-19	13:00	Fine	CMA1b_1hr_3 140336	2.6620	2.6679	13090.17	13091.17	1.00	1.19	1.19	1.19	72	82.4

Location: CMA2a - Causeway Bay Community Centre

Report on 24-hour TSP monitoring Action Level (μg/m3) - 169.5 Limit Level (μg/m3) - 260

Date	Sampling	Weather	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling		w Rate, m <sup>3</sup> /ı	min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, Q <sub>si</sub>	Final, $Q_{sf}$	Average	Volume, m <sup>3</sup>	$\mu g/m^3$
27-Dec-18	8:00	Cloudy	CMA2a_24hr 140127	2.6686	2.8381	22493.59	22517.59	24.00	1.30	1.31	1.31	1885	89.9
2-Jan-19	8:00	Cloudy	CMA2a_24hr 140182	2.6681	2.8377	22520.59	22544.59	24.00	1.32	1.32	1.32	1904	89.1
8-Jan-19	8:00	Fine	CMA2a_24hr 140167	2.6392	2.8878	22547.59	22571.59	24.00	1.31	1.31	1.31	1890	131.5
15-Jan-19	14:10	Cloudy	CMA2a_24hr 140289	2.6747	2.8391	22577.61	22601.61	24.00	1.31	1.32	1.31	1890	87.0
18-Jan-19	8:00	Fine	CMA2a_24hr 140289	2.6822	2.8965	22601.61	22625.61	24.00	1.32	1.31	1.31	1891	113.3
23-Jan-19	8:00	Fine	CMA2a_24hr 140311	2.6680	2.9149	22628.61	22652.61	24.00	1.32	1.31	1.32	1895	130.3

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 14 January 2019 to 15 January 2019.

Report on 1-hour TSP monitoring Action Level (μg/m3) - 323.4 Limit Level (μg/m3) - 500

Date	Sampling	Weather	Filter paper no.	Filter Weigh	nt, g	Elapse Time, h	r	Sampling	Flo	w Rate, m <sup>3</sup> /i	min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, Q <sub>si</sub>	Final, Q <sub>sf</sub>	Average	Volume, m <sup>3</sup>	μg/m <sup>3</sup>
28-Dec-18	8:15	Cloudy	CMA2a_1hr_1 140011	2.6860	2.6927	22517.59	22518.59	1.00	1.31	1.31	1.31	79	85.0
28-Dec-18	9:17	Cloudy	CMA2a_1hr_2 140013	2.6713	2.6781	22518.59	22519.59	1.00	1.31	1.31	1.31	79	86.3
28-Dec-18	10:20	Cloudy	CMA2a_1hr_3 140014	2.6924	2.7045	22519.59	22520.59	1.00	1.31	1.31	1.31	79	153.5
3-Jan-19	8:03	Cloudy	CMA2a_1hr_1 140179	2.6627	2.6673	22544.59	22545.59	1.00	1.32	1.32	1.32	79	58.1
3-Jan-19	10:25	Cloudy	CMA2a_1hr_2 206798	2.6883	2.6920	22545.59	22546.59	1.00	1.32	1.32	1.32	79	46.7
3-Jan-19	13:00	Cloudy	CMA2a_1hr_3 206787	2.6851	2.6906	22546.59	22547.59	1.00	1.32	1.32	1.32	79	69.5
9-Jan-19	9:25	Fine	CMA2a_1hr_1 140217	2.6570	2.6686	22571.60	22572.60	1.00	1.31	1.31	1.31	79	147.2
9-Jan-19	11:00	Fine	CMA2a_1hr_2 140226	2.6838	2.6954	22572.60	22573.60	1.00	1.31	1.31	1.31	79	147.2
9-Jan-19	13:00	Fine	CMA2a_1hr_3 140233	2.6701	2.6846	22573.60	22574.60	1.00	1.31	1.31	1.31	79	183.9
15-Jan-19	8:00	Cloudy	CMA2a_1hr_1 140240	2.6724	2.6859	22574.61	22575.61	1.00	1.31	1.31	1.31	79	171.8
15-Jan-19	10:00	Cloudy	CMA2a_1hr_2 140264	2.6812	2.6882	22575.61	22576.61	1.00	1.31	1.31	1.31	79	89.1
15-Jan-19	13:00	Cloudy	CMA2a_1hr_3 140273	2.6718	2.6793	22576.61	22577.61	1.00	1.31	1.31	1.31	79	95.5
19-Jan-19	8:03	Fine	CMA2a_1hr_1 140240	2.6759	2.6871	22625.61	22626.61	1.00	1.31	1.31	1.31	79	142.5
19-Jan-19	9:50	Fine	CMA2a_1hr_2 140264	2.6577	2.6670	22626.61	22627.61	1.00	1.31	1.31	1.31	79	118.3
19-Jan-19	13:00	Fine	CMA2a_1hr_3 140273	2.6649	2.6731	22627.61	22628.61	1.00	1.31	1.31	1.31	79	104.3
24-Jan-19	9:05	Fine	CMA2a_1hr_1 140317	2.6547	2.6693	22652.61	22653.61	1.00	1.31	1.31	1.31	79	185.1
24-Jan-19	10:58	Fine	CMA2a_1hr_2 140328	2.6769	2.6891	22653.61	22654.61	1.00	1.31	1.31	1.31	79	154.7
24-Jan-19	13:00	Fine	CMA2a_1hr_3 140335	2.6480	2.6610	22654.61	22655.61	1.00	1.31	1.31	1.31	79	164.8

Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring Action Level (µg/m3) - 171 Limit Level (µg/m3) - 260

Date	Sampling	Weather	Filter paper no.	Filter Weigh	nt, g	Elapse Tim	ə, hr	Sampling	Flo	w Rate, m <sup>3</sup> /	min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, $Q_{si}$	Final, Q <sub>sf</sub>	Average	Volume, m <sup>3</sup>	<sup>β</sup> μg/m <sup>3</sup>
27-Dec-18	8:00	Cloudy	CMA3a_24hr 140126	2.6605	2.6968	9930.76	9954.76	24.00	1.26	1.26	1.26	1815	20.0
2-Jan-19	8:00	Cloudy	CMA3a_24hr 140180	2.6646	2.7144	9957.76	9981.76	24.00	1.27	1.27	1.27	1830	27.2
8-Jan-19	8:00	Fine	CMA3a_24hr 140169	2.6320	2.7432	9984.78	10008.78	24.00	1.26	1.26	1.26	1819	61.1
14-Jan-19	8:00	Cloudy	CMA3a_24hr 140239	2.6649	2.7704	10011.80	10035.80	24.00	1.29	1.29	1.29	1857	56.8
18-Jan-19	8:00	Fine	CMA3a_24hr 140239	2.6724	2.7835	10038.80	10062.80	24.00	1.27	1.26	1.26	1820	61.1
23-Jan-19	8:00	Fine	CMA3a_24hr 140310	2.6638	2.8270	10065.80	10089.80	24.00	1.27	1.26	1.27	1823	89.5

Report on 1-hour TSP monitoring Action Level (µg/m3) - 311.3 Limit Level (µg/m3) - 500

Date	Sampling	Weather	Filter paper no.	Filter Weigl	nt, g	Elapse Tim	ə, hr	Sampling	Flo	w Rate, m <sup>3</sup> /r	min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, Q <sub>si</sub>	Final, Q <sub>sf</sub>	Average	Volume, m <sup>3</sup>	μg/m <sup>3</sup>
28-Dec-18	10:45	Cloudy	CMA3a_1hr_1 140144	2.6711	2.6746	9954.76	9955.76	1.00	1.32	1.32	1.32	79	44.1
28-Dec-18	13:00	Cloudy	CMA3a_1hr_2 140147	2.6561	2.6608	9955.76	9956.76	1.00	1.32	1.32	1.32	79	59.3
28-Dec-18	14:06	Cloudy	CMA3a_1hr_3 140148	2.6389	2.6477	9956.76	9957.76	1.00	1.29	1.29	1.29	78	113.4
3-Jan-19	8:45	Cloudy	CMA3a_1hr_1 140177	2.6663	2.6699	9981.76	9982.76	1.00	1.36	1.36	1.36	81	44.3
3-Jan-19	10:15	Cloudy	CMA3a_1hr_2 206797	2.6939	2.6955	9982.76	9983.76	1.00	1.30	1.30	1.30	78	20.6
3-Jan-19	13:00	Cloudy	CMA3a_1hr_3 206807	2.7119	2.7188	9983.76	9984.76	1.00	1.27	1.27	1.27	76	90.6
9-Jan-19	9:10	Fine	CMA3a_1hr_1 140215	2.6575	2.6631	10008.78	10009.78	1.00	1.32	1.32	1.32	79	70.6
9-Jan-19	10:50	Fine	CMA3a_1hr_2 140225	2.6591	2.6647	10009.78	10010.78	1.00	1.32	1.32	1.32	79	70.6
9-Jan-19	13:00	Fine	CMA3a_1hr_3 140232	2.6624	2.6701	10010.78	10011.78	1.00	1.32	1.32	1.32	79	97.1
15-Jan-19	9:10	Cloudy	CMA3a_1hr_1 140300	2.6742	2.6779	10035.80	10036.80	1.00	1.32	1.32	1.32	79	46.8
15-Jan-19	10:30	Cloudy	CMA3a_1hr_2 140268	2.6662	2.6719	10036.80	10037.80	1.00	1.32	1.32	1.32	79	72.1
15-Jan-19	13:00	Cloudy	CMA3a_1hr_3 140275	2.6690	2.6717	10037.80	10038.80	1.00	1.32	1.32	1.32	79	34.1
19-Jan-19	8:30	Fine	CMA3a_1hr_1 140300	2.6740	2.6773	10062.80	10063.80	1.00	1.26	1.26	1.26	76	43.6
19-Jan-19	9:40	Fine	CMA3a_1hr_2 140268	2.6796	2.6834	10063.80	10064.80	1.00	1.26	1.26	1.26	76	50.2
19-Jan-19	13:00	Fine	CMA3a_1hr_3 140275	2.6573	2.6603	10064.80	10065.80	1.00	1.26	1.26	1.26	76	39.6
24-Jan-19	8:45	Fine	CMA3a_1hr_1 140316	2.6700	2.6744	10089.80	10090.80	1.00	1.26	1.26	1.26	76	58.0
24-Jan-19	10:47	Fine	CMA3a_1hr_2 140327	2.6707	2.6765	10090.80	10091.80	1.00	1.26	1.26	1.26	76	76.4
24-Jan-19	13:00	Fine	CMA3a_1hr_3 140334	2.6750	2.6813	10091.80	10092.80	1.00	1.26	1.26	1.26	76	83.0

Location: CMA4a - SPCA

Report on 24-hour TSP monitoring Action Level (μg/m3) - 171.. Limit Level (μg/m3) - 260 171.2

Date	Sampling	Weather	Filter paper no.	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m <sup>3</sup> /i	min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, $Q_{si}$	Final, $Q_{sf}$	Average	Volume, m <sup>3</sup>	μg/m³
27-Dec-18	8:00	Cloudy	CMA4a_24hr 140125	2.6717	2.7864	26749.26	26773.26	24.00	1.25	1.26	1.26	1810	63.4
2-Jan-19	8:00	Cloudy	CMA4a_24hr 140161	2.6511	2.7712	26776.26	26800.26	24.00	1.27	1.27	1.27	1824	65.8
8-Jan-19	8:00	Fine	CMA4a_24hr 140168	2.6545	2.8186	26803.26	26827.26	24.00	1.26	1.26	1.26	1814	90.5
14-Jan-19	8:00	Cloudy	CMA4a_24hr 140238	2.6732	2.8009	26830.27	26854.27	24.00	1.26	1.26	1.26	1811	70.5
19-Jan-19	13:00	Fine	CMA4a_24hr 140238	2.6839	2.7769	26860.27	26884.27	24.00	1.26	1.26	1.26	1815	51.2
23-Jan-19	8:00	Fine	CMA4a_24hr 140379	2.6528	2.8463	26884.27	26908.27	24.00	1.26	1.26	1.26	1818	106.4
Remarks: Due to	o interruption of	electricity, the	nr TSP was rescheduled from 18 January 2019 to 19 January 2019.										· · · · ·

Report on 1-hour TSP monitoring Action Level (µg/m3) - 312 Limit Level (µg/m3) - 500 312.5 500

Date	Sampling	Weather	Filter paper no.	Filter Weigh	nt, g	Elapse Tim	ə, hr	Sampling	Flo	w Rate, m <sup>3</sup> /	min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, $Q_{si}$	Final, Q <sub>sf</sub>	Average	Volume, m <sup>3</sup>	μg/m <sup>3</sup>
28-Dec-18	11:00	Cloudy	CMA4a_1hr_1 140145	2.6552	2.6620	26773.26	26774.26	1.00	1.26	1.26	1.26	76	89.9
28-Dec-18	13:00	Cloudy	CMA4a_1hr_2 140146	2.6508	2.6577	26774.26	26775.26	1.00	1.26	1.26	1.26	76	91.2
28-Dec-18	14:20	Cloudy	CMA4a_1hr_3 140149	2.6500	2.6597	26775.26	26776.26	1.00	1.26	1.26	1.26	76	128.2
3-Jan-19	8:30	Cloudy	CMA4a_1hr_1 140178	2.6624	2.6664	26800.26	26801.26	1.00	1.27	1.27	1.27	76	52.7
3-Jan-19	10:10	Cloudy	CMA4a_1hr_2 206796	2.6787	2.6803	26801.26	26802.26	1.00	1.27	1.27	1.27	76	21.1
3-Jan-19	13:00	Cloudy	CMA4a_1hr_3 206806	2.7197	2.7254	26802.26	26803.26	1.00	1.27	1.27	1.27	76	75.1
9-Jan-19	9:10	Fine	CMA4a_1hr_1 140214	2.6683	2.6765	26827.27	26828.27	1.00	1.26	1.26	1.26	76	108.4
9-Jan-19	10:47	Fine	CMA4a_1hr_2 140224	2.6507	2.6592	26828.27	26829.27	1.00	1.26	1.26	1.26	76	112.4
9-Jan-19	13:00	Fine	CMA4a_1hr_3 140231	2.6621	2.6717	26829.27	26830.27	1.00	1.26	1.26	1.26	76	126.9
15-Jan-19	9:10	Cloudy	CMA4a_1hr_1 140260	2.6769	2.6830	26854.27	26855.27	1.00	1.26	1.26	1.26	75	80.8
15-Jan-19	10:30	Cloudy	CMA4a_1hr_2 140267	2.6808	2.6865	26855.27	26856.27	1.00	1.26	1.26	1.26	75	75.5
15-Jan-19	13:00	Cloudy	CMA4a_1hr_3 140276	2.6732	2.6771	26856.27	26857.27	1.00	1.26	1.26	1.26	75	51.7
19-Jan-19	8:00	Fine	CMA4a_1hr_1 140260	2.6720	2.6823	26857.27	26858.27	1.00	1.26	1.26	1.26	75	136.4
19-Jan-19	9:25	Fine	CMA4a_1hr_2 140267	2.6795	2.6859	26858.27	26859.27	1.00	1.26	1.26	1.26	75	84.8
19-Jan-19	10:40	Fine	CMA4a_1hr_3 140276	2.6828	2.6904	26859.27	26860.27	1.00	1.26	1.26	1.26	75	100.7
24-Jan-19	8:30	Fine	CMA4a_1hr_1 140378	2.6673	2.6776	26908.27	26909.27	1.00	1.26	1.26	1.26	76	136.1
24-Jan-19	10:43	Fine	CMA4a_1hr_2 140326	2.6602	2.6689	26909.27	26910.27	1.00	1.26	1.26	1.26	76	115.0
24-Jan-19	13:00	Fine	CMA4a_1hr_3 140333	2.6581	2.6673	26910.27	26911.27	1.00	1.26	1.26	1.26	76	121.6

Location: CMA5b - Pedestrian Plaza

Report on 24-hour TSP monitoring Action Level (µg/m3) - 181 Limit Level (µg/m3) - 260

Date	Sampling	Weather	Filter paper no.	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m <sup>3</sup> /ı	min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, $Q_{si}$	Final, $Q_{sf}$	Average	Volume, m <sup>3</sup>	μg/m <sup>3</sup>
27-Dec-18	8:00	Cloudy	CMA5b_24hr 140124	2.6363	2.7417	11379.91	11403.91	24.00	1.24	1.25	1.24	1792	58.8
2-Jan-19	8:00	Cloudy	CMA5b_24hr 140156	2.6446	2.7532	11406.91	11430.91	24.00	1.23	1.23	1.23	1767	61.5
8-Jan-19	8:00	Fine	CMA5b_24hr 140163	2.6507	2.7864	11433.92	11457.92	24.00	1.22	1.22	1.22	1756	77.3
14-Jan-19	8:00	Cloudy	CMA5b_24hr 140235	2.6765	2.8150	11460.92	11484.92	24.00	1.27	1.27	1.27	1833	75.6
18-Jan-19	8:00	Fine	CMA5b_24hr 140235	2.6826	2.8523	11487.92	11511.92	24.00	1.31	1.33	1.32	1897	89.5
23-Jan-19	8:00	Fine	CMA5b_24hr 140386	2.6604	2.8024	11514.92	11538.92	24.00	1.22	1.22	1.22	1760	80.7

Report on 1-hour TSP monitoring Action Level (µg/m3) - 332 Limit Level (µg/m3) - 500 332 500

Date	Sampling	Weather	Filter paper no.	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m <sup>3</sup> /r	min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, $Q_{si}$	Final, $Q_{sf}$	Average	Volume, m <sup>3</sup>	μg/m³
28-Dec-18	13:00	Cloudy	CMA5b_1hr_1 140143	2.6612	2.6707	11403.91	11404.91	1.00	1.22	1.22	1.22	73	129.7
28-Dec-18	14:34	Cloudy	CMA5b_1hr_2 140140	2.6459	2.6590	11404.91	11405.91	1.00	1.22	1.22	1.22	73	178.8
28-Dec-18	15:45	Cloudy	CMA5b_1hr_3 140154	2.6635	2.6737	11405.91	11406.91	1.00	1.22	1.22	1.22	73	139.3
3-Jan-19	8:40	Cloudy	CMA5b_1hr_1 140171	2.6551	2.6597	11430.92	11431.92	1.00	1.23	1.23	1.23	74	62.6
3-Jan-19	10:40	Cloudy	CMA5b_1hr_2 206800	2.6914	2.6938	11431.92	11432.92	1.00	1.23	1.23	1.23	74	32.6
3-Jan-19	13:40	Cloudy	CMA5b_1hr_3 206765	2.6920	2.6928	11432.92	11433.92	1.00	1.23	1.23	1.23	74	10.9
9-Jan-19	8:05	Fine	CMA5b_1hr_1 140208	2.6609	2.6675	11457.92	11458.92	1.00	1.28	1.28	1.28	77	86.2
9-Jan-19	9:48	Fine	CMA5b_1hr_2 140218	2.6588	2.6686	11458.92	11459.92	1.00	1.28	1.28	1.28	77	128.0
9-Jan-19	13:00	Fine	CMA5b_1hr_3 140228	2.6729	2.6864	11459.92	11460.92	1.00	1.28	1.28	1.28	77	176.3
15-Jan-19	9:20	Cloudy	CMA5b_1hr_1 140261	2.6860	2.6915	11484.92	11485.92	1.00	1.27	1.27	1.27	76	72.0
15-Jan-19	10:38	Cloudy	CMA5b_1hr_2 140269	2.6828	2.6888	11485.92	11486.92	1.00	1.30	1.30	1.30	78	76.9
15-Jan-19	13:00	Cloudy	CMA5b_1hr_3 140277	2.6638	2.6720	11486.92	11487.92	1.00	1.30	1.30	1.30	78	105.1
19-Jan-19	8:37	Fine	CMA5b_1hr_1 140261	2.6632	2.6705	11511.92	11512.92	1.00	1.27	1.27	1.27	76	95.5
19-Jan-19	10:15	Fine	CMA5b_1hr_2 140269	2.6627	2.6753	11512.92	11513.92	1.00	1.27	1.27	1.27	76	164.9
19-Jan-19	13:00	Fine	CMA5b_1hr_3 140277	2.6530	2.6609	11513.92	11514.92	1.00	1.25	1.25	1.25	75	105.7
24-Jan-19	8:02	Fine	CMA5b_1hr_1 140313	2.6541	2.6632	11538.92	11539.92	1.00	1.33	1.33	1.33	80	113.8
24-Jan-19	9:52	Fine	CMA5b_1hr_2 140319	2.6538	2.6665	11539.92	11540.92	1.00	1.30	1.30	1.30	78	162.2
24-Jan-19	13:00	Fine	CMA5b_1hr_3 140330	2.6561	2.6670	11540.92	11541.92	1.00	1.33	1.33	1.33	80	136.3

Location: CMA6a - WD2 PRE Office

### Report on 24-hour TSP monitoring

Action Level -	187.3	µg/m3	
Limit Level -	260	μg/m3	

Date	Sampling	Weather	Filter paper no.	Filter Weigh	nt, g	Elapse Tim	ə, hr	Sampling	Flo	w Rate, m <sup>3</sup> /r	min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, $Q_{si}$	Final, $Q_{sf}$	Average	Volume, m <sup>3</sup>	μg/m <sup>3</sup>
27-Dec-18	8:00	Cloudy	CMA6a_24hr 140120	2.6547	2.7480	5046.13	5070.13	24.00	1.14	1.15	1.15	1651	56.5
2-Jan-19	8:00	Cloudy	CMA6a_24hr 140157	2.6492	2.7634	5073.13	5097.13	24.00	1.16	1.16	1.16	1668	68.5
8-Jan-19	8:00	Fine	CMA6a_24hr 140188	2.6653	2.8472	5100.15	5124.15	24.00	1.15	1.15	1.15	1656	109.9
14-Jan-19	8:00	Cloudy	CMA6a_24hr 140237	2.6633	2.7592	5127.16	5151.16	24.00	1.15	1.15	1.15	1656	57.9
18-Jan-19	8:00	Fine	CMA6a_24hr 140237	2.6850	2.7753	5154.16	5178.16	24.00	1.28	1.15	1.22	1750	51.6
23-Jan-19	8:00	Fine	CMA6a_24hr 140309	2.6807	2.8136	5181.17	5205.17	24.00	1.15	1.15	1.15	1660	80.0


### Report on 1-hour TSP monitoring Action Level - $300.1 \mu$ g/m<sup>3</sup>

Limit Level - 500  $\mu$  g/m3

Date	Sampling	Weather	Filter paper no.	Filter Weigl	nt, g	Elapse Tim	ə, hr	Sampling	Flo	w Rate, m <sup>3</sup> /i	min	Total	TSP Level,
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, $Q_{si}$	Final, $Q_{sf}$	Average	Volume, m <sup>a</sup>	<sup>3</sup> μg/m³
28-Dec-18	13:08	Cloudy	CMA6a_1hr_1 140142	2.6640	2.6683	5070.13	5071.13	1.00	1.15	1.15	1.15	69	62.3
28-Dec-18	14:16	Cloudy	CMA6a_1hr_2 140141	2.6318	2.6386	5071.13	5072.13	1.00	1.15	1.15	1.15	69	98.5
28-Dec-18	15:30	Cloudy	CMA6a_1hr_3 140152	2.6553	2.6607	5072.13	5073.13	1.00	1.15	1.15	1.15	69	78.2
3-Jan-19	9:00	Cloudy	CMA6a_1hr_1 140172	2.6479	2.6507	5097.13	5098.13	1.00	1.16	1.16	1.16	69	40.4
3-Jan-19	10:50	Cloudy	CMA6a_1hr_2 206802	2.7060	2.7070	5098.13	5099.13	1.00	1.16	1.16	1.16	69	14.4
3-Jan-19	13:00	Cloudy	CMA6a_1hr_3 206767	2.6838	2.6838	5099.13	5100.13	1.00	1.16	1.16	1.16	69	<0.1
9-Jan-19	8:10	Fine	CMA6a_1hr_1 140210	2.6531	2.6576	5124.15	5125.15	1.00	1.15	1.15	1.15	69	65.2
9-Jan-19	10:00	Fine	CMA6a_1hr_2 140220	2.6626	2.6697	5125.15	5126.15	1.00	1.15	1.15	1.15	69	102.8
9-Jan-19	13:00	Fine	CMA6a_1hr_3 140230	2.6668	2.6742	5126.15	5127.15	1.00	1.15	1.15	1.15	69	107.2
15-Jan-19	9:30	Cloudy	CMA6a_1hr_1 140263	2.6693	2.6724	5151.16	5152.16	1.00	1.15	1.15	1.15	69	45.0
15-Jan-19	10:50	Cloudy	CMA6a_1hr_2 140271	2.6739	2.6773	5152.16	5153.16	1.00	1.21	1.21	1.21	73	46.8
15-Jan-19	13:00	Cloudy	CMA6a_1hr_3 140279	2.6826	2.6853	5153.16	5154.16	1.00	1.18	1.18	1.18	71	38.2
19-Jan-19	8:50	Fine	CMA6a_1hr_1 140263	2.6775	2.6831	5178.16	5179.16	1.00	1.15	1.15	1.15	69	81.3
19-Jan-19	10:35	Fine	CMA6a_1hr_2 140271	2.6616	2.6643	5179.16	5180.16	1.00	1.15	1.15	1.15	69	39.2
19-Jan-19	13:00	Fine	CMA6a_1hr_3 140279	2.6499	2.6527	5180.16	5181.16	1.00	1.15	1.15	1.15	69	40.7
24-Jan-19	8:05	Fine	CMA6a_1hr_1 140314	2.6739	2.6822	5205.17	5206.17	1.00	1.22	1.22	1.22	73	113.7
24-Jan-19	9:45	Fine	CMA6a_1hr_2 140322	2.6504	2.6559	5206.17	5207.17	1.00	1.15	1.15	1.15	69	79.6
24-Jan-19	13:00	Fine	CMA6a_1hr_3 140332	2.6561	2.6618	5207.17	5208.17	1.00	1.28	1.28	1.28	77	74.2




**Graphic Presentation of 1 hour TSP Result** 

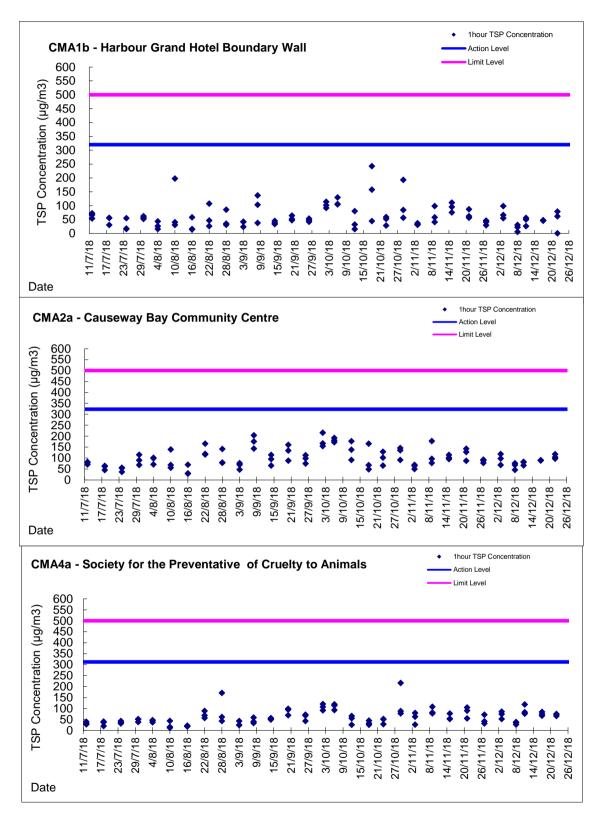





**Graphic Presentation of 1 hour TSP Result** 

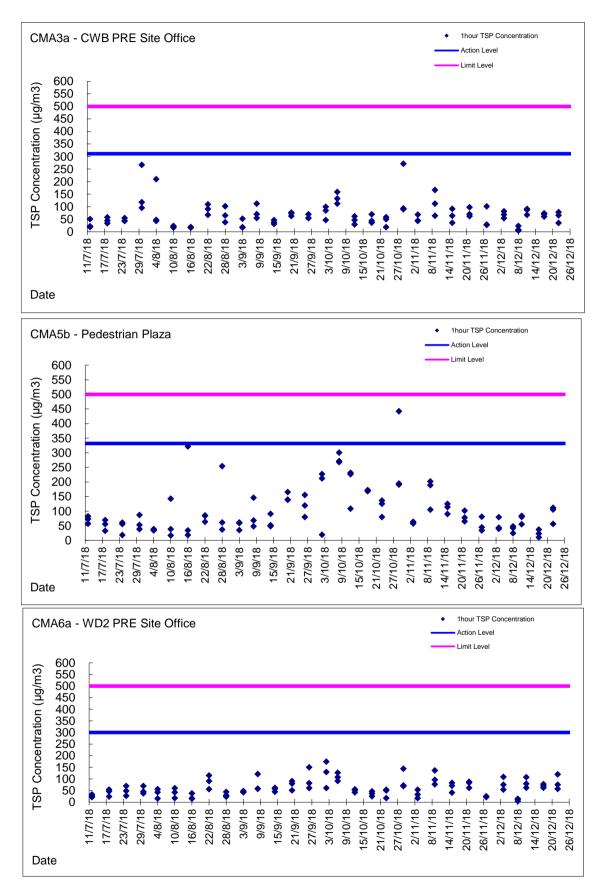




**Graphic Presentation of 24 hour TSP Result** 

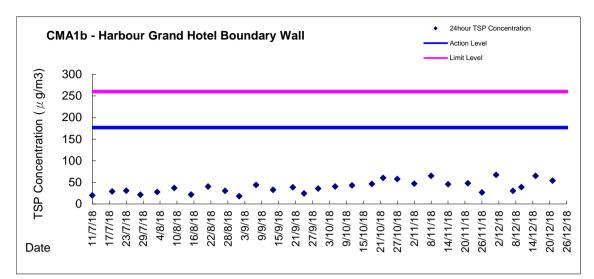


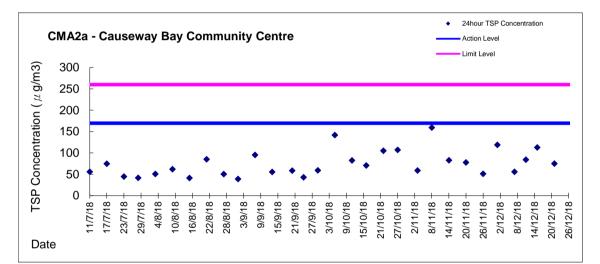


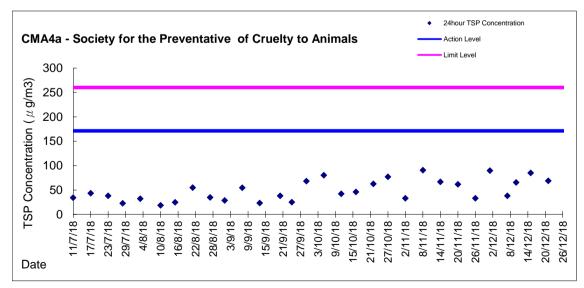




**Graphic Presentation of 24 hour TSP Result** 

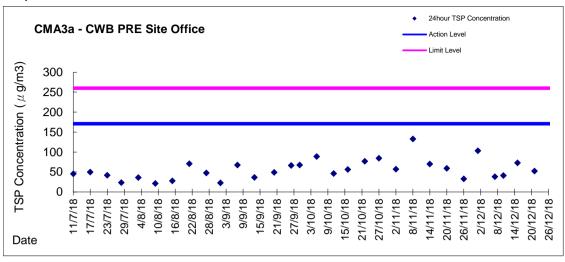

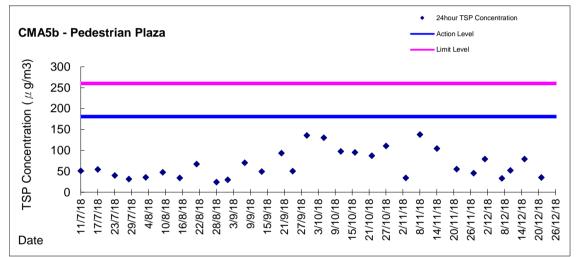

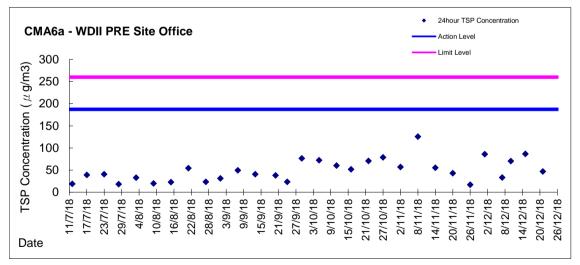



Appendix 5.4

Water Quality Monitoring Results and Graphical Presentations

Water Monitoring Result at C1 - HKCEC Extension Mid-Flood Tide

Date	Time	Weater Condition		ng Depth	Wat	er Temp °C	erature		pH			Salinit ppt	Ξy	D	O Satur	ation		DO ma/L			Turbic NTU			led Solids a/L
		Contailion	r	n	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	alue	Average	Value	Average
27/12/18	11:05	Cloudy	Middle	3.0	20.90	20.90	20.90	7.31	7.31	7.31	33.38	33.38	33.38	67.8	68.9	69.1	4.98	5.06	5.08	4.80	4.81	4.80	7	7.50
	11:07		Middle	3.0	20.90	20.90		7.31	7.31		33.38	33.38		69.7	70.0		5.12	5.14		4.80	4.80		8	
29/12/18	9:50	Fine	Middle	2.5	19.60	19.60	19.50	7.07	7.07	7.07	33.60	33.60	33.60	72.1	72.3	71.9	5.43	5.44	5.43	4.76	4.77	4.79	6	6.00
	9:52		Middle	2.5	19.40	19.40		7.07	7.07		33.60	33.60		71.6	71.6		5.40	5.46		4.81	4.81		6	
31/12/18	14:50	Fine	Middle	3.0	18.90	18.90	18.90	6.87	6.87	6.87	33.80	33.80	33.80	75.8	76.4	76.5	5.76	5.80	5.81	3.40	3.40	3.40	6	6.00
	14:52		Middle	3.0	18.90	18.90		6.87	6.87		33.80	33.80		76.9	76.8		5.84	5.83		3.41	3.40		6	
2/1/19	11:40	Cloudy	Middle	3.0	18.40	18.40	18.35	6.74	6.74	6.74	33.73	33.73	33.73	77.3	77.4	77.5	5.94	5.96	5.96	4.08	4.00	4.02	5	5.00
	11:42		Middle	3.0	18.30	18.30		6.74	6.74		33.73	33.73		77.6	77.6		5.97	5.97		4.00	4.00		5	
4/1/19	17:00	Fine	Middle	3.0	19.30	19.30	19.30	7.90	7.90	7.91	33.76	33.76	33.76	92.6	92.5	92.5	6.99	6.98	6.98	4.08	4.01	4.02	3	3.00
	17:02		Middle	3.0	19.30	19.30		7.91	7.91		33.76	33.76		92.4	92.5		6.98	6.98		4.00	4.00		3	
7/1/19	7:55	Cloudy	Middle	3.0	18.80	18.80	18.80	8.05	8.05	8.05	33.46	33.46	33.46	85.1	85.0	84.6	6.49	6.49	6.47	4.28	4.28	4.28	6	6.00
	7:57		Middle	3.0	18.80	18.80		8.05	8.05		33.46	33.46		85.2	83.0		6.51	6.40		4.29	4.27		6	
9/1/19	10:50	Cloudy	Middle	3.0	18.40	18.40	18.40	8.21	8.21	8.21	33.28	33.28	33.28	91.3	91.4	91.3	7.04	7.04	7.03	6.05	6.06	6.05	3	2.50
	10:52		Middle	3.0	18.40	18.40		8.21	8.21		33.28	33.28		91.3	91.1		7.03	7.02		6.05	6.03		2	
11/1/19	10:20	Cloudy	Middle	3.0	19.70	19.70	19.70	8.10	8.10	8.11	32.66	32.66	32.66	101.8	101.6	101.1	7.67	7.66	7.62	7.51	7.42	7.46	6	5.50
	10:22		Middle	3.0	19.70	19.70		8.11	8.11		32.66	32.66		100.4	100.6		7.57	7.57		7.44	7.46		5	
14/1/19	13:10	Cloudy	Middle	3.0	19.10	19.10	19.10	8.67	8.67	8.68	32.25	32.25	32.25	91.8	92.1	92.2	7.02	7.04	7.05	2.82	2.83	2.84	4	4.00
	13:12		Middle	3.0	19.10	19.10		8.68	8.68		32.25	32.25		92.5	92.5		7.07	7.08		2.85	2.85		4	
16/1/19	13:05	Cloudy	Middle	3.0	19.80	19.80	19.80	8.63	8.63	8.64	32.03	32.03	32.03	102.4	102.0	101.6	7.74	7.71	7.68	0.98	0.97	0.97	7	6.50
	13:07		Middle	3.0	19.80	19.80		8.64	8.64		32.03	32.03		101.0	100.9		7.64	7.63		0.96	0.96		6	
18/1/19	13:30	Cloudy	Middle	3.0	18.70	18.70	18.70	8.66	8.66	8.67	31.86	31.86	31.87	88.8	88.9	88.7	6.85	6.87	6.85	2.45	2.45	2.48	4	5.00
	13:32		Middle	3.0	18.70	18.70		8.67	8.67		31.87	31.87		88.4	88.8		6.83	6.83		2.51	2.52		6	<u> </u>
21/1/19	7:34	Cloudy	Middle	2.5	18.00	18.00	18.00	7.80	7.80	7.80	31.05	31.05	31.05	78.8	79.3	78.9	6.20	6.23	6.20	2.92	2.87	2.86	5	5.50
	7:35		Middle	2.5	18.00	18.00		7.80	7.80		31.05	31.05		79.1	78.4		6.22	6.16		2.84	2.80		6	
23/1/19	9:35	Fine	Middle	3.0	17.80	17.80	17.75	8.34	8.34	8.34	31.27	31.27	31.27	96.2	96.3	96.2	7.59	7.60	7.59	2.10	2.10	2.12	5	5.50
	9:37		Middle	3.0	17.70	17.70		8.34	8.34		31.27	31.27		96.0	96.1		7.57	7.58		2.12	2.16		6	
25/1/19	14:40	Fine	Middle	3.0	20.40	20.40	20.40	8.16	8.16	8.17	31.17	31.17	31.17	107.0	102.1	103.1	7.66	7.66	7.64	3.01	3.04	3.03	9	9.50
	14:42		Middle	3.0	20.40	20.40		8.17	8.17		31.17	31.17		101.7	101.5		7.61	7.61		3.04	3.04		10	

### Water Monitoring Result at P1 - HKCEC Phase I Mid-Flood Tide

Date	Time	Weater Condition		ng Depth	Wat	er Temp °C	erature		pН			Salinit ppt	ty	C	O Satur	ration		DO ma/L			Turbid NTU	ity	Suspend	led Solids
		Contailion	r	n	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	alue	Average	Va	lue	Average	Va	alue	Average	Value	Average
27/12/18	10:45	Cloudy	Middle	3.0	21.00	21.00	21.05	7.27	7.27	7.28	33.26	33.26	33.26	71.2	71.6	70.9	5.23	5.25	5.19	4.97	4.97	4.97	7	6.50
27712710	10:47	cloudy	Middle	3.0	21.10	21.10	21.00	7.28	7.28		33.26	33.26	00.20	70.2	70.4		5.13	5.14	0.10	4.97	4.98		6	0.00
29/12/18	9:30	Fine	Middle	2.5	19.00	19.00	19.00	6.89	6.89	6.89	32.56	32.56	32.56	75.5	74.9	74.3	5.79	5.78	5.71	5.63	5.61	5.61	6	6.00
	9:32		Middle	2.5	19.00	19.00		6.89	6.89		32.56	32.56		73.1	73.5		5.63	5.65		5.60	5.60		6	
31/12/18	14:30	Fine	Middle	3.0	18.90	18.90	18.85	6.82	6.82	6.83	33.76	33.76	33.76	76.6	76.9	76.9	5.83	5.86	5.86	3.95	3.94	3.94	3	3.00
	14:32		Middle	3.0	18.80	18.80		6.84	6.84		33.75	33.75		77.1	77.1		5.87	5.87		3.94	3.94		3	
2/1/19	11:15	Cloudy	Middle	3.0	18.20	18.20	18.20	6.53	6.53	6.57	33.34	33.34	33.34	76.9	77.6	77.8	5.94	6.00	6.01	4.31	4.29	4.27	4	4.00
	11:17		Middle	3.0	18.20	18.20		6.61	6.61		33.34	33.34		78.3	78.3		6.05	6.05		4.23	4.23		4	
4/1/19	16:40	Fine	Middle	3.0	20.00	20.00	20.05	7.69	7.69	7.70	33.81	33.81	33.81	92.2	93.0	92.9	6.86	6.91	6.91	3.76	3.70	3.70	3	3.00
	16:42	-	Middle	3.0	20.10	20.10		7.71	7.71	-	33.80	33.80		93.1	93.2		6.92	6.93		3.67	3.66		3	
7/1/19	7:30	Cloudy	Middle	3.0	18.90	18.90	18.90	7.95	7.95	7.96	33.53	33.53	33.53	86.3	86.4	86.3	6.57	6.58	6.57	4.74	4.77	4.76	5	5.50
	7:32		Middle	3.0	18.90	18.90		7.96	7.96		33.53	33.53		86.3	86.1		6.57	6.56		4.77	4.75		6	
9/1/19	10:30	Cloudy	Middle	3.0	18.80	1.80	14.60	8.06	8.06	8.07	33.35	33.35	33.35	95.7	95.6	95.0	7.30	7.30	7.25	5.38	5.39	5.37	2	2.00
	10:32		Middle	3.0	18.90	18.90		8.07	8.07		33.35	33.35		94.2	94.3		7.19	7.19		5.37	5.34		2	
11/1/19	10:00	Cloudy	Middle	3.0	19.90	19.90	19.90	7.62	7.62	7.66	32.69	32.69	32.69	102.2	102.2	101.5	7.67	7.67	7.62	4.23	4.23	4.23	3	3.00
	10:02		Middle	3.0	19.90	19.90		7.69	7.69		32.68	32.68		100.8	100.9		7.56	7.57		4.23	4.23		3	
14/1/19	12:50	Cloudy	Middle	3.0	19.20	19.20	19.25	8.62	8.62	8.63	32.29	32.29	32.29	100.2	100.1	99.4	7.64	7.62	7.57	1.86	1.92	1.91	3	3.00
	12:52		Middle	3.0	19.30	19.30		8.64	8.64		32.29	32.29		98.9	98.5		7.52	7.50		1.93	1.94		3	
16/1/19	12:45	Cloudy	Middle	4.0	19.80	19.80	19.85	8.37	8.37	8.48	31.94	31.94	31.95	95.5	95.6	95.3	7.21	7.21	7.20	1.04	1.06	1.06	4	3.50
	12:47		Middle	4.0	19.90	19.90		8.59	8.59		31.95	31.95		95.0	95.1		7.18	7.18		1.07	1.07		3	
18/1/19	13:10	Cloudy	Middle	3.0	18.50	18.50	18.50	8.21	8.21	8.25	31.62	31.62	31.62	100.9	101.0	100.5	7.83	7.84	7.79	2.03	2.03	2.03	6	5.00
	13:12		Middle	3.0	18.50	18.50		8.29	8.29		31.61	31.61		100.0	100.0		7.75	7.75		2.02	2.02		4	
21/1/19	7:05	Cloudy	Middle	2.5	18.00	18.00	18.00	7.77	7.77	7.77	30.15	30.15	30.15	70.2	70.4	70.3	5.55	5.56	5.55	4.88	5.07	5.01	5	5.00
	7:06	,	Middle	2.5	18.00	18.00		7.77	7.77		30.15	30.15		70.4	70.0		5.57	5.53		5.02	5.05		5	
23/1/19	9:15	Fine	Middle	3.0	17.60	17.60	17.60	8.23	8.23	8.24	31.22	31.22	31.22	95.5	95.3	95.2	7.56	7.56	7.55	2.32	2.32	2.32	4	4.00
	9:17		Middle	3.0	17.60	17.60		8.24	8.24		31.22	31.22		94.9	95.2		7.52	7.54		2.32	2.32		4	
25/1/19	14:20	Fine	Middle	3.0	20.10	20.10	20.20	7.88	7.88	7.92	31.17	31.17	31.17	99.9	99.5	99.6	7.52	7.49	7.49	2.74	2.59	2.60	8	9.00
	14:22		Middle	3.0	20.30	20.30		7.95	7.95		31.17	31.17		99.4	99.5		7.48	7.48		2.53	2.53		10	

#### Water Monitoring Result at P3 - APA Mid-Flood Tide

Date	Time	Weater Condition	Samplin	* '	Wat	er Temp °C	perature		pH -			Salini ppt	ty	D	O Satur	ation		DO ma/L			Turbid NTU	ity	Suspend	led Solids a/l
		Contaition	n	n	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Value	Average
27/12/18	10:50	Cloudy	Middle	3.0	20.80	20.80	20.80	7.28	7.28	7.29	33.37	33.37	33.38	71.6	71.7	71.9	5.27	5.27	5.29	4.82	4.81	4.81	4	4.00
27/12/10	10:52	Cloudy	Middle	3.0	20.80	20.80	20.00	7.29	7.29	7.25	33.38	33.38	33.30	72.2	72.2	71.5	5.31	5.32	5.25	4.80	4.80	4.01	4	4.00
29/12/18	9:35	Fine	Middle	2.5	19.20	19.20	19.10	6.95	6.95	6.97	33.63	33.63	33.64	73.6	74.8	74.7	5.61	5.68	5.68	5.28	5.28	5.31	3	3.00
20/12/10	9:37	1 110	Middle	2.5	19.00	19.00	10.10	6.99	6.99	0.07	33.64	33.64	00.04	75.2	75.2	74.7	5.72	5.72	0.00	5.34	5.34	0.01	3	0.00
31/12/18	14:35	Fine	Middle	3.0	18.50	18.50	18.50	6.82	6.82	6.82	33.80	33.80	33.80	75.1	75.7	76.0	5.76	5.80	5.83	3.51	3.52	3.51	3	3.00
51/12/10	14:37	TING	Middle	3.0	18.50	18.50	10.50	6.82	6.82	0.02	33.80	33.80	55.50	76.4	76.7	70.0	5.86	5.88	5.65	3.51	3.51	0.01	3	0.00
2/1/19	11:20	Cloudy	Middle	3.0	18.00	18.00	18.00	6.66	6.66	6.67	33.80	33.80	33.80	75.6	76.1	76.3	5.84	5.88	5.89	4.66	4.62	4.62	6	6.00
2/1/10	11:22	oloudy	Middle	3.0	18.00	18.00	10.00	6.68	6.68	0.07	33.80	33.80	00.00	76.6	76.7	70.0	5.92	5.93	0.00	4.60	4.58	4.62	6	0.00
4/1/19	16:45	Fine	Middle	3.0	19.50	19.50	19.55	7.75	7.75	7.76	33.82	33.82	33.82	92.9	92.3	92.0	6.98	6.93	6.91	3.66	3.65	3.65	3	3.00
1110	16:47	1 110	Middle	3.0	19.60	19.60	10.00	7.76	7.76	1.10	33.81	33.81	00.02	91.2	91.5	02.0	6.85	6.87	0.01	3.65	3.65	0.00	3	0.00
7/1/19	7:35	Cloudy	Middle	3.0	18.70	18.70	18.75	7.98	7.98	7.98	33.51	33.51	33.51	87.0	87.2	86.7	6.65	6.66	6.63	4.60	4.63	4.63	4	4.50
11113	7:37	oloudy	Middle	3.0	18.80	18.80	10.75	7.98	7.98	7.00	33.51	33.51	00.01	86.2	86.4	00.7	6.59	6.60	0.00	4.64	4.65	4.00	5	4.50
9/1/19	10:35	Cloudy	Middle	3.0	18.60	18.60	18.60	8.10	8.10	8.11	33.32	33.32	33.32	89.6	89.7	89.3	6.87	6.87	6.85	5.41	5.40	5.40	3	3.00
6, 1, 10	10:37	cloudy	Middle	3.0	18.60	18.60	10.00	8.11	8.11	0.111	33.32	33.32	00.02	89.0	89.0	00.0	6.82	6.82	0.00	5.39	5.38	0.10	3	0.00
11/1/19	10:05	Cloudy	Middle	3.0	19.60	19.60	19.65	7.82	7.82	7.84	32.66	32.66	32.67	100.6	101.1	100.7	7.59	7.63	7.60	6.78	6.76	6.72	3	3.50
	10:07	cloudy	Middle	3.0	19.70	19.70	10.00	7.85	7.85		32.67	32.67	02:07	100.5	100.7		7.58	7.60		6.66	6.67	0.72	4	0.00
14/1/19	12:55	Cloudy	Middle	3.0	19.10	19.10	19.10	8.64	8.64	8.65	32.27	32.27	32.27	93.7	93.9	93.3	7.16	7.17	7.13	2.80	2.71	2.73	3	3.50
	12:57		Middle	3.0	19.10	19.10		8.65	8.65		32.27	32.27		92.8	92.9		7.08	7.10		2.70	2.71		4	
16/1/19	12:50	Cloudy	Middle	3.0	19.50	19.50	19.50	8.51	8.51	8.52	31.93	31.93	31.93	93.1	93.0	93.2	7.07	7.07	7.07	1.50	1.50	1.51	3	3.50
	12:52		Middle	3.0	19.50	19.50		8.52	8.52		31.93	31.93		93.1	93.4		7.09	7.05		1.51	1.52		4	
18/1/19	13:15	Cloudy	Middle	3.0	18.30	18.30	18.30	8.46	8.46	8.46	31.92	31.92	31.92	107.2	106.7	111.4	8.34	8.31	8.68	1.79	1.78	1.77	6	5.00
	13:17		Middle	3.0	18.30	18.30		8.46	8.46		31.92	31.92		115.7	115.8		9.03	9.04		1.77	1.74		4	
21/1/19	7:11	Cloudy	Middle	2.5	18.00	18.00	18.00	7.77	7.77	7.77	30.66	30.66	30.66	74.0	74.5	73.9	5.83	5.87	5.82	4.83	4.71	4.69	4	3.50
	7:12		Middle	2.5	18.00	18.00		7.77	7.77		30.66	30.66		73.5	73.6		5.79	5.80		4.73	4.49		3	
23/1/19	9:20	Fine	Middle	3.0	17.40	17.40	17.40	8.28	8.28	8.28	31.24	31.24	31.24	93.7	94.0	93.7	7.44	7.47	7.44	2.16	2.16	2.16	5	5.00
	9:22		Middle	3.0	17.40	17.40		8.28	8.28		31.24	31.24		93.9	93.1		7.46	7.40		2.16	2.16		5	
25/1/19	14:25	Fine	Middle	3.0	19.30	19.30	19.35	8.08	8.08	8.09	31.13	31.13	31.13	96.0	97.4	97.4	7.39	7.46	7.47	2.38	2.33	2.34	10	10.50
	14:27		Middle	3.0	19.40	19.40		8.10	8.10		31.13	31.13		97.8	98.4		7.48	7.53		2.34	2.32		11	

#### Water Monitoring Result at P4 - SOC Mid-Flood Tide

Date	Time	Weater Condition	Samplin	ig Depth	Wat	er Temp	erature		pН			Salini ppt	ty	D	O Satur	ation		DO mg/L			Turbid NTU	ity	Suspend	ed Solids
		Condition	r	n	Va	llue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	alue	Average	Value	Average
27/12/18	10:55	Cloudy	Middle	3.0	20.90	20.90	20.90	7.30	7.30	7.30	33.39	33.39	33.39	69.5	69.7	70.0	5.11	5.12	5.15	4.83	4.82	4.82	8	8.50
27/12/16	10:57	Cloudy	Middle	3.0	20.90	20.90	20.90	7.30	7.30	7.30	33.39	33.39	33.39	70.3	70.4	70.0	5.17	5.18	5.15	4.81	4.81	4.02	9	8.50
29/12/18	9:40	Fine	Middle	2.5	19.50	19.50	19.40	7.04	7.04	7.04	33.58	33.58	33.58	72.5	72.7	72.6	5.48	5.49	5.49	4.58	4.57	4.57	3	3.00
	9:42		Middle	2.5	19.30	19.30		7.04	7.04		33.58	33.58		72.7	72.3		5.50	5.47		4.56	4.55		3	
31/12/18	14:40	Fine	Middle	3.0	19.00	19.00	19.00	6.85	6.85	6.86	33.77	33.77	33.77	77.8	77.7	77.6	5.91	5.90	5.89	3.41	3.42	3.43	6	6.00
	14:42	-	Middle	3.0	19.00	19.00		6.86	6.86		33.77	33.77		77.4	77.4		5.88	5.88		3.44	3.46		6	
2/1/19	11:25	Cloudy	Middle	3.0	18.50	18.50	18.45	6.71	6.71	6.75	33.79	33.79	33.79	76.2	76.5	76.5	5.84	5.87	5.87	4.01	4.01	4.01	4	4.00
	11:27		Middle	3.0	18.40	18.40		6.78	6.78		33.79	33.79		76.7	76.5		5.89	5.89		4.00	4.00		4	
4/1/19	16:50	Fine	Middle	3.0	19.30	19.30	19.35	7.80	7.80	7.82	33.76	33.76	33.76	90.3	90.0	90.7	6.86	6.79	6.85	3.57	3.52	3.51	3	3.00
	16:52		Middle	3.0	19.40	19.40		7.84	7.84		33.76	33.76		91.2	91.1		6.87	6.87		3.48	3.47		3	
7/1/19	7:40	Cloudy	Middle	3.0	18.80	18.80	18.80	8.00	8.00	8.01	33.48	33.48	33.48	86.6	86.7	86.7	6.61	6.61	6.61	4.50	4.46	4.45	5	5.00
	7:42		Middle	3.0	18.80	18.80		8.02	8.02		33.48	33.48		86.6	86.7		6.60	6.61		4.44	4.41		5	
9/1/19	10:40	Cloudy	Middle	3.0	18.50	18.50	18.50	8.14	8.14	8.15	33.31	33.31	33.31	87.5	88.2	88.2	6.72	6.77	6.77	5.43	5.36	5.35	<2	3.00
	10:42		Middle	3.0	18.50	18.50		8.15	8.15		33.31	33.31		88.7	88.5		6.81	6.79		5.32	5.30		3	
11/1/19	10:10	Cloudy	Middle	3.0	19.70	19.70	19.75	7.92	7.92	7.95	32.68	32.68	32.68	96.6	96.7	96.7	7.27	7.27	7.27	6.80	6.81	6.81	6	6.00
	10:12		Middle	3.0	19.80	19.80		7.98	7.98		32.67	32.67		96.6	96.7		7.27	7.27		6.80	6.81		6	
14/1/19	13:00	Cloudy	Middle	3.0	19.10	19.10	19.10	8.65	8.65	8.66	32.18	32.18	32.21	93.2	93.1	92.7	7.12	7.11	7.08	1.96	1.96	1.95	3	3.00
	13:02		Middle	3.0	19.10	19.10		8.66	8.66		32.24	32.24		92.1	92.2		7.03	7.05		1.90	1.96		3	
16/1/19	12:55	Cloudy	Middle	3.0	19.30	19.30	19.30	8.53	8.53	8.53	31.99	31.99	32.00	94.5	94.5	94.6	7.20	7.21	7.21	1.48	1.47	1.47	6	6.00
	12:57		Middle	3.0	19.30	19.30		8.53	8.53		32.00	32.00		94.6	94.6		7.21	7.21		1.48	1.44		6	
18/1/19	13:20	Cloudy	Middle	3.0	18.40	18.40	18.40	8.58	8.58	8.59	31.90	31.90	31.93	88.5	88.5	88.5	6.86	6.86	6.85	1.71	1.72	1.73	4	4.50
	13:22		Middle	3.0	18.40	18.40		8.60	8.60		31.96	31.96		88.4	88.4		6.84	6.84		1.74	1.74		5	
21/1/19	7:16 7:17	Cloudy	Middle Middle	2.5 2.5	17.90 17.90	17.90 17.90	17.90	7.78 7.78	7.78 7.78	7.78	30.66 30.66	30.66	30.66	70.2 72.4	72.5 71.8	71.7	5.55 5.72	5.73	5.67	3.30 3.28	3.41 3.15	3.29	6	6.00
	9:25		Middle	3.0	17.90	17.90		8.30	8.33		30.66	30.66 31.26		72.4 96.3	95.7		7.63	5.67 7.59		2.10	2.10		5	
23/1/19	9:23	Fine	Middle	3.0	17.50	17.50	17.55	8.31	8.31	8.31	31.20	31.20	31.27	95.8	95.7 96.4	96.1	7.59	7.39	7.57	2.10	2.10	2.10	5	5.00
	14:30		Middle	3.0	19.50	19.50		8.10	8.10		31.18	31.18		99.7	99.8		7.48	7.40		2.09	2.03		9	
25/1/19	14:32	Fine	Middle	3.0	19.60	19.60	19.55	8.11	8.11	8.11	31.18	31.18	31.18	99.6	99.9	99.8	7.47	7.48	7.48	2.66	2.66	2.68	10	9.50
	17.02	1	widule	0.0	10.00	10.00		0.11	0.11	1	51.10	01.10	1	55.0	55.5		·.+/	1.40		2.00	2.00		10	1

### Water Monitoring Result at P5 - WCT / RT / IT Mid-Flood Tide

Date	Time	Weater Condition		ng Depth	Wat	er Temp °C	perature		pH			Salinit ppt	Ξ <b>y</b>	C	O Satur	ration		DO ma/L			Turbid NTU		Suspend	led Solids
		Contailion	r	n	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	alue	Average		
27/12/18	11:00	Cloudy	Middle	3.0	20.80	20.80	20.80	7.31	7.31	7.31	33.41	33.41	33.41	68.9	68.9	69.1	5.07	5.07	5.09	4.78	4.78	4.78	9	9.00
27/12/10	11:02	Cibudy	Middle	3.0	20.80	20.80	20.00	7.31	7.31	7.51	33.41	33.41	33.41	69.3	69.4	03.1	5.09	5.11	5.09	4.78	4.79	4.70	9	5.00
29/12/18	9:45	Fine	Middle	2.5	19.50	19.50	19.45	7.04	7.04	7.05	33.51	33.51	33.55	71.7	72.4	72.5	5.40	5.47	5.47	4.23	4.25	4.26	4	3.50
20,12,10	9:47	T IIIC	Middle	2.5	19.40	19.40	10.40	7.06	7.06	7.00	33.58	33.58	66.66	73.2	72.8	72.0	5.52	5.49	0.47	4.27	4.29	4.20	3	0.00
31/12/18	14:45	Fine	Middle	3.0	19.00	19.00	19.05	6.87	6.87	6.87	33.80	33.80	33.80	76.9	76.8	76.5	5.84	5.83	5.84	3.40	3.40	3.40	7	6.50
01712,10	14:47	1 110	Middle	3.0	19.10	19.10	10.00	6.87	6.87	0.07	33.80	33.80	00.00	76.3	76.0	70.0	5.86	5.84	0.04	3.40	3.41	0.40	6	0.00
2/1/19	11:30	Cloudy	Middle	3.0	18.50	18.50	18.45	6.74	6.74	6.74	33.80	33.80	33.81	76.3	76.5	76.8	5.86	5.87	5.90	4.09	4.10	4.09	5	5.50
2, .,	11:32	cloudy	Middle	3.0	18.40	18.40	10.10	6.74	6.74	0.7.1	33.81	33.81	00.01	77.0	77.2	1010	5.93	5.93	0.00	4.09	4.08		6	0.00
4/1/19	16:55	Fine	Middle	3.0	19.20	19.20	19.20	7.86	7.86	7.87	33.78	33.78	33.78	90.5	90.5	90.3	6.84	6.84	6.82	4.11	4.03	4.06	4	3.50
	16:57		Middle	3.0	19.20	19.20		7.87	7.87		33.78	33.78		90.0	90.1		6.80	6.81		4.05	4.05		3	
7/1/19	7:50	Cloudy	Middle	3.0	18.80	18.80	18.80	8.03	8.03	8.04	33.47	33.47	33.47	95.2	95.3	95.1	7.26	7.27	7.25	4.11	4.10	4.10	4	4.50
	7:52		Middle	3.0	18.80	18.80		8.04	8.04		33.47	33.47		94.9	95.0		7.24	7.24		4.09	4.10		5	
9/1/19	10:45	Cloudy	Middle	3.0	18.50	18.50	18.50	8.18	8.18	8.19	33.31	33.31	33.31	89.1	89.4	89.7	6.85	6.87	6.90	5.26	5.23	5.23	3	3.50
	10:47		Middle	3.0	18.50	18.50		8.19	8.19		33.30	33.30		90.1	90.3		6.93	6.94		5.20	5.21		4	
11/1/19	10:15	Cloudy	Middle	3.0	19.60	19.60	19.60	8.03	8.03	8.04	32.67	32.67	32.67	103.1	103.2	102.7	7.78	7.79	7.75	7.09	7.07	7.10	7	6.50
	10:17		Middle	3.0	19.60	19.60		8.05	8.05		32.67	32.67		102.0	102.5		7.70	7.74	-	7.11	7.12		6	
14/1/19	13:05	Cloudy	Middle	3.0	19.10	19.10	19.10	8.66	8.66	8.66	32.21	32.21	32.23	90.3	90.0	90.7	6.90	6.88	6.93	2.36	2.47	2.43	3	3.50
	13:07		Middle	3.0	19.10	19.10		8.66	8.66		32.25	32.25		91.5	90.9		6.99	6.94		2.41	2.46		4	
16/1/19	13:00	Cloudy	Middle	3.0	19.20	19.20	19.20	8.54	8.54	8.54	31.95	31.95	31.96	95.1	95.6	95.5	7.30	7.31	7.31	1.43	1.43	1.43	6	5.50
	13:02		Middle	3.0	19.20	19.20		8.54	8.54		31.96	31.96		95.7	95.7		7.31	7.31		1.41	1.43		5	
18/1/19	13:25	Cloudy	Middle	3.0	18.70	18.70	18.70	8.63	8.63	8.64	31.92	31.92	31.92	93.3	92.0	91.9	7.20	7.10	7.09	2.37	2.38	2.37	4	4.00
	13:27	,	Middle	3.0	18.70	18.70		8.65	8.65		31.92	31.92		91.1	91.1		7.03	7.03		2.36	2.36	_	4	
21/1/19	7:23	Cloudy	Middle	2.5	18.00	18.00	18.00	7.79	7.79	7.79	31.07	31.07	31.07	74.7	74.5	74.1	5.87	5.85	5.82	3.21	3.28	3.17	6	6.50
	7:24		Middle	2.5	18.00	18.00		7.79	7.79		31.07	31.07		74.1	73.0		5.82	5.73		3.05	3.12		7	
23/1/19	9:30	Fine	Middle	3.0	17.70	17.70	17.70	8.33	8.33	8.33	31.26	31.26	31.26	95.0	95.3	95.2	7.49	7.54	7.51	2.10	2.10	2.13	6	6.00
	9:32		Middle	3.0	17.70	17.70		8.33	8.33		31.26	31.26		95.2	95.1		7.51	7.51		2.16	2.16		6	
25/1/19	14:35	Fine	Middle	3.0	20.00	20.00	20.05	8.13	8.13	8.13	31.18	31.18	31.18	100.2	100.1	100.2	7.57	7.56	7.57	2.46	2.48	2.47	16	<u>15.50</u>
	14:37	-	Middle	3.0	20.10	20.10		8.13	8.13		31.18	31.18		100.1	100.2		7.56	7.57	-	2.50	2.44		15	



### Water Monitoring Result at RW21-P789 - GEC / CRB / SHK Mid-Flood Tide

Date	Time	Weater Condition		ig Depth	Wat	er Temp °C	erature		рH			Salini ppt	ty	D	O Satur	ation		DO ma/L			Turbid NTU		Suspend	led Solids
		Contailion	r	n	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Va	alue	Average	Value	Average
27/12/18	11:15	Cloudy	Middle	4.0	21.20	21.20	21.20	7.29	7.29	7.30	33.41	33.41	33.41	74.8	75.1	74.7	5.46	5.49	5.46	6.46	6.47	6.47	8	8.00
	11:17	-	Middle	4.0	21.20	21.20		7.30	7.30		33.41	33.41		74.6	74.4		5.44	5.43		6.48	6.48		8	<u> </u>
29/12/18	10:05	Fine	Middle	4.0	19.70	19.70	19.60	7.12	7.12	7.15	33.43	33.43	33.43	78.4	78.6	78.2	5.90	5.91	5.89	5.10	5.08	5.13	4	3.50
	10:07		Middle	4.0	19.50	19.50		7.17	7.17		33.43	33.43		78.0	77.7		5.88	5.86		5.16	5.16		3	<u> </u>
31/12/18	15:15	Fine	Middle	4.0	19.30	19.30	19.20	6.82	6.82	6.85	33.35	33.35	32.85	80.3	79.2	79.2	6.13	6.04	6.04	2.64	2.63	2.64	4	3.50
	15:17		Middle	4.0	19.10	19.10		6.87	6.87		32.35	32.35		78.7	78.7		6.00	6.00		2.66	2.64		3	<u> </u>
2/1/19	11:55	Cloudy	Middle	4.0	18.40	18.40	18.40	6.80	6.80	6.81	33.22	33.22	33.22	74.5	74.9	74.8	5.74	5.77	5.76	4.42	4.38	4.40	9	9.50
	11:57		Middle	4.0	18.40	18.40		6.81	6.81		33.22	33.22		75.1	74.7		5.78	5.76		4.38	4.43		10	<u> </u>
4/1/19	14:50	Fine	Middle	4.0	20.00	20.00	20.00	7.73	7.73	7.75	32.98	32.98	32.98	93.2	93.0	92.6	6.98	6.94	6.91	4.96	4.86	4.90	4	4.00
	14:52		Middle	4.0	20.00	20.00		7.76	7.76		32.98	32.98		92.2	92.0		6.87	6.86		4.88	4.89		4	<u> </u>
7/1/19	8:15	Cloudy	Middle	4.0	19.20	19.20	19.20	7.89	7.89	7.91	33.60	33.60	33.60	91.2	90.8	90.5	6.90	6.87	6.85	4.77	4.79	4.80	6	6.00
	8:17		Middle	4.0	19.20	19.20		7.92	7.92		33.60	33.60		90.1	90.0		6.81	6.81		4.80	4.83		6	<u> </u>
9/1/19	11:15	Cloudy	Middle	4.0	18.80	18.80	18.75	8.24	8.24	8.24	33.20	33.20	33.20	86.6	86.8	86.4	6.62	6.66	6.62	4.89	4.90	4.90	2	2.00
	11:17		Middle	4.0	18.70	18.70		8.24	8.24		33.20	33.20		86.0	86.2		6.58	6.60		4.91	4.91		2	<u> </u>
11/1/19	11:00	Cloudy	Middle	4.0	19.90	19.90	19.95	7.30	7.32	7.31	32.53	32.53	32.53	103.2	103.4	102.3	7.72	7.74	7.65	4.70	4.72	4.73	5	5.00
	11:02		Middle	4.0	20.00	20.00		7.30	7.32		32.52	32.52		101.5	101.1		7.58	7.55		4.74	4.75		5	<u> </u>
14/1/19	10:40	Cloudy	Middle	4.0	19.40	19.40	19.45	8.51	8.51	8.52	32.09	32.09	32.09	93.6	93.2	93.1	7.11	7.07	7.07	7.21	7.24	7.25	5	5.00
	10:42		Middle	4.0	19.50	19.50		8.53	8.53		32.09	32.09		92.8	92.7		7.04	7.04		7.27	7.27		5	<u> </u>
16/1/19	13:30	Cloudy	Middle	4.0	19.30	19.30	19.30	8.66	8.66	8.66	31.95	31.95	31.96	96.0	96.0	96.1	7.32	7.32	7.33	2.94	2.93	2.93	7	6.50
	13:32		Middle	4.0	19.30	19.30		8.66	8.66		31.96	31.96		96.1	96.2		7.33	7.34		2.93	2.92		6	<u> </u>
18/1/19	14:00 14:02	Cloudy	Middle	4.0	18.40 18.40	18.40 18.40	18.40	8.68 8.69	8.68 8.69	8.69	31.86 31.86	31.86 31.86	31.86	87.1 85.7	87.4 85.8	86.5	6.77 6.68	6.78 6.69	6.73	4.34 4.59	4.46 4.58	4.49	10	10.00
	3:30		Middle	4.0 3.5	18.40	18.40		8.69 7.77	7.77		31.86	31.86		85.7 78.9	85.8 78.4		6.22	6.18		4.59 3.50	4.58 3.44		4	<u> </u>
21/1/19	3:30	Cloudy	Middle	3.5	17.90	17.90	17.90	7.77	7.77	7.77	30.87	30.87	30.87	78.9	78.4	78.2	6.17	6.10	6.17	3.50	3.44	3.45	5	4.50
	9:50		Middle	4.0	17.30	18.10		8.29	8.29		31.25	31.25		96.5	96.5		7.57	7.57		2.35	2.36		5	<u> </u>
23/1/19	9:52	Fine	Middle	4.0	18.10	18.10	18.10	8.31	8.31	8.30	31.25	31.25	31.25	95.5	95.5	96.0	7.49	7.49	7.53	2.36	2.36	2.36	5	5.00
	13:55		Middle	4.0	19.90	19.90		8.16	8.16		31.08	31.08		98.4	98.2		7.46	7.44		3.01	3.01		14	<u> </u>
25/1/19	13:57	Fine	Middle	4.0	19.90	19.90	19.90	8.17	8.17	8.17	31.08	31.08	31.08	98.7	98.9	98.6	7.48	7.50	7.47	3.02	3.03	3.02	12	13.00

Water Monitoring Result at WSD19 - Sheung Wan Mid-Flood Tide

Date	Time	Weater Condition	Samplin	ig Depth	Wat	er Temp °C	perature		pH			Salinit	ty	D	O Satur	ation		DO mg/L			Turbid NTU		Suspend	ed Solids
		Condition	r	n	Va	lue	Average	Va	lue -	Average	Va	ppt lue	Average	Va	lue	Average	Va		Average	Va	alue	Average	Value	Average
27/12/18	9:40	Cloudy	Middle	4.0	21.20	21.20	21.20	6.91	6.91	6.93	33.16	33.16	33.16	66.9	67.1	66.4	4.89	4.91	4.85	7.98	7.97	7.96	9	8.50
27/12/10	9:42	Cloudy	Middle	4.0	21.20	21.20	21.20	6.94	6.94	0.00	33.16	33.16	33.10	65.7	65.7	00.4	4.81	4.80	4.00	7.93	7.94	7.00	8	0.00
29/12/18	10:30	Fine	Middle	4.0	19.70	19.70	19.55	7.16	7.16	7.20	33.68	33.68	33.68	84.2	82.0	81.9	6.34	6.17	6.16	6.21	6.23	6.30	7	7.00
	10:32		Middle	4.0	19.40	19.40		7.23	7.23		33.68	33.68		80.7	80.6		6.07	6.06		6.37	6.37		7	
31/12/18	13:30	Fine	Middle	3.5	19.60	19.60	19.55	6.71	6.71	6.71	33.45	33.45	33.45	73.0	73.1	74.2	5.49	5.49	5.58	6.01	6.03	6.05	6	5.50
	13:32		Middle	3.5	19.50	19.50		6.71	6.71		33.44	33.44		75.2	75.4		5.66	5.68		6.06	6.08		5	
2/1/19	12:15	Cloudy	Middle	4.0	18.70	18.70	18.65	6.82	6.82	6.83	33.62	33.62	33.62	76.7	77.1	77.1	5.88	5.91	5.90	5.33	5.34	5.35	4	4.00
	12:17		Middle	4.0	18.60	18.60		6.83	6.83		33.62	33.62		77.5	77.2		5.90	5.91		5.37	5.37		4	
4/1/19	13:45	Fine	Middle	3.5	19.90	19.90	19.90	7.32	7.32	7.33	33.63	33.63	33.63	92.6	91.4	91.2	6.92	6.85	6.82	7.94	7.93	7.93	8	8.00
	13:47		Middle	3.5	19.90	19.90		7.33	7.33		33.62	33.62		90.7	90.2		6.77	6.73		7.93	7.90		8	<u> </u>
7/1/19	9:20	Cloudy	Middle	4.0	18.90	18.90	18.90	8.03	8.03	8.04	33.52	33.52	33.52	88.1	87.8	87.9	6.71	6.69	6.70	5.24	5.27	5.26	6	6.00
	9:22		Middle	4.0	18.90	18.90		8.04	8.04		33.52	33.52		88.0	87.6		6.71	6.68		5.27	5.26		6	<u> </u>
9/1/19	8:40	Cloudy	Middle	4.0	19.20	19.20	19.20	7.55	7.55	7.62	33.22	33.22	33.22	86.9	87.1	86.8	6.59	6.61	6.58	6.90	6.89	6.88	6	5.50
	8:42		Middle	4.0	19.20	19.20		7.69	7.69		33.21	33.21		86.6	86.4		6.57	6.55		6.87	6.86		5	
11/1/19	12:00	Cloudy	Middle	4.0	20.10	20.10	20.20	8.02	8.02	8.05	32.68	32.68	32.68	100.5	100.6	99.8	7.50	7.51	7.45	6.42	6.44	6.45	8	7.50
	12:02		Middle	4.0	20.30	20.30		8.07	8.07		32.68	32.68		99.0	99.1		7.38	7.39		6.47	6.47		7	
14/1/19	11:40	Cloudy	Middle	3.0	19.40	19.40	19.45	8.57	8.57	8.58	32.35	32.35	32.42	88.0	86.5	86.7	6.68	6.57	6.57	2.50	2.51	2.47	5	4.50
	11:42 13:50		Middle Middle	3.0 4.0	19.50 18.90	19.50 18.90		8.59 8.07	8.59 8.07		32.60 32.07	32.36 32.07		86.1 92.4	86.1 92.2		6.52 7.10	6.52 7.09		2.43 1.82	2.42		4	<u> </u>
16/1/19	13:50	Cloudy	Middle	4.0	18.90	18.90	18.90	8.07	8.07	8.07	32.07	32.07	32.07	92.4	92.2	92.3	7.10	7.09	7.10	1.82	1.64	1.74	4	4.00
	15:00		Middle	4.0	18.80	18.80		8.64	8.64		31.98	31.98		97.9	97.7		7.54	7.52		2.44	2.41		6	
18/1/19	15:02	Cloudy	Middle	4.0	18.80	18.80	18.80	8.65	8.65	8.65	31.98	31.98	31.98	96.3	96.5	97.1	7.41	7.43	7.48	2.44	2.32	2.37	4	5.00
	4:02		Middle	3.5	18.00	18.00		7.74	7.74		31.84	31.84		78.0	78.6		6.10	6.15		5.97	5.76		8	<u> </u>
21/1/19	4:03	Cloudy	Middle	3.5	18.00	18.00	18.00	7.74	7.74	7.74	31.84	31.84	31.84	79.2	81.6	79.4	6.19	6.39	6.21	5.40	5.53	5.67	6	7.00
	7:45		Middle	4.0	17.00	17.00		8.24	8.24		31.26	31.26		91.8	92.0		7.36	7.36		3.05	3.00		6	
23/1/19	7:47	Fine	Middle	4.0	17.00	17.00	17.00	8.25	8.25	8.25	31.25	31.25	31.26	92.0	92.1	92.0	7.36	7.37	7.36	2.99	2.98	3.01	4	5.00
	15:00		Middle	3.5	19.30	19.30		8.10	8.10		31.14	31.14		96.3	97.1		7.37	7.43		3.06	3.13		11	
25/1/19	15:02	Fine	Middle	3.5	19.40	19.40	19.35	8.10	8.10	8.10	31.14	31.14	31.14	97.3	97.7	97.1	7.46	7.47	7.43	3.13	3.13	3.11	10	10.50

Water Monitoring Result at C1 - HKCEC Mid-Ebb Tide

Date	Time	Weater Condition		ig Depth	Wat	er Temp °C	perature		pH -			Salinit ppt	у	C	O Satur	ation		DO ma/L			Turbid NTU		Suspend	ded Solids
		Condition	r	n	Va	lue	Average	Va	lue	Average	Va		Average	Va	lue	Average	Va	lue	Average	Va	alue	Average	Value	Average
27/12/18	4:27	Cloudy	Middle	2.5	20.70	20.70	20.70	8.18	8.18	8.18	33.05	33.05	33.05	74.7	75.1	75.6	5.52	5.54	5.58	1.27	1.34	1.26	4	4.50
21/12/10	4:28	Cloudy	Middle	2.5	20.70	20.70	20.70	8.18	8.18	0.10	33.05	33.05	00.00	76.4	76.3	70.0	5.64	5.63	0.00	1.26	1.15	1.20	5	4.00
29/12/18	4:32	Cloudy	Middle	3.0	18.90	18.90	18.90	8.18	8.18	8.18	33.32	33.32	33.32	76.7	77.3	77.1	5.86	5.91	5.89	1.27	1.31	1.32	6	5.50
20/12/10	4:34	cicady	Middle	3.0	18.90	18.90	10.00	8.18	8.18	0.110	33.32	33.32	00.02	77.4	77.0		5.91	5.89	0.00	1.37	1.34		5	0.00
31/12/18	8:15	Cloudy	Middle	3.0	17.90	17.90	17.90	8.21	8.21	8.21	33.30	33.30	33.30	75.0	76.9	76.5	5.85	6.00	5.97	1.44	1.48	1.40	<2	2.00
01712710	8:16	cicady	Middle	3.0	17.90	17.90		8.21	8.21	0.2.1	33.30	33.30	00.00	77.5	76.4	70.0	6.05	5.98	0.07	1.31	1.35		2	2.00
2/1/19	1:04	Cloudy	Middle	2.5	17.70	17.70	17.70	8.62	8.62	8.62	33.04	33.04	33.04	86.3	87.5	86.9	6.75	6.83	6.79	5.14	5.16	5.14	4	4.00
2/1/10	1:05	cicady	Middle	2.5	17.70	17.70		8.62	8.62	0.02	33.04	33.04	00.01	87.1	86.6	00.0	6.80	6.77	0.10	5.20	5.06	0.111	4	
4/1/19	3:01	Cloudy	Middle	2.5	19.20	19.20	19.20	8.59	8.59	8.59	32.91	32.91	32.91	87.1	87.5	87.3	6.61	6.65	6.63	5.08	5.02	5.27	5	5.00
	3:02	cicady	Middle	2.5	19.20	19.20	10.20	8.59	8.59	0.00	32.91	32.91	02.01	87.7	86.8	07.10	6.66	6.59	0.00	5.97	4.99	0.127	5	0.00
7/1/19	3:17	Cloudy	Middle	2.5	18.30	18.30	18.30	8.65	8.65	8.65	32.31	32.31	32.31	78.4	79.4	78.8	6.09	6.16	6.12	4.54	4.51	4.60	2	2.50
11110	3:18	Cloudy	Middle	2.5	18.30	18.30	10.00	8.65	8.65	0.00	32.31	32.31	02.01	79.0	78.3	70.0	6.13	6.08	0.12	4.65	4.68	4.00	3	2.00
9/1/18	3:52	Cloudy	Middle	2.5	18.80	18.80	18.80	8.67	8.67	8.67	32.86	32.86	32.86	93.1	91.9	92.1	7.00	6.90	6.91	5.86	5.79	5.79	4	3.50
	3:53	,	Middle	2.5	18.80	18.80		8.67	8.67		32.86	32.86		92.5	90.9		6.91	6.83		5.69	5.82		3	
11/1/19	5:38	Cloudy	Middle	2.5	18.60	18.60	18.60	8.68	8.68	8.68	32.48	32.48	32.48	91.7	92.6	92.1	7.06	7.13	7.09	5.80	5.84	5.86	3	3.00
	5:39		Middle	2.5	18.60	18.60		8.68	8.68		32.48	32.48		92.3	91.8		7.11	7.07		5.88	5.92		3	
14/1/19	4:15	Cloudy	Middle	3.0	18.80	18.80	18.80	8.61	8.61	8.61	32.27	32.27	32.27	92.5	93.2	92.6	7.11	7.16	7.12	1.67	1.51	1.55	<2	2.00
	4:16	,	Middle	3.0	18.80	18.80		8.61	8.61		32.27	32.27	-	92.9	91.9		7.14	7.06		1.53	1.48		2	
16/1/19	22:13	Cloudy	Middle	3.0	18.00	18.00	18.00	8.66	8.67	8.67	31.93	31.93	31.93	82.8	84.2	84.8	6.48	6.57	6.63	1.45	1.49	1.43	3	3.00
	22:14	,	Middle	3.0	18.00	18.00		8.67	8.67		31.93	31.93		86.2	85.8		6.74	6.71		1.30	1.48		3	
18/1/19	22:12	Cloudy	Middle	3.0	19.10	19.10	19.10	7.80	7.80	7.80	32.14	32.14	32.14	83.4	84.5	83.8	6.27	6.35	6.29	2.94	2.92	3.00	4	4.00
	22:13	,	Middle	3.0	19.10	19.10		7.80	7.80		32.14	32.14	-	83.9	83.2		6.30	6.25		3.04	3.11		4	
21/1/19	1:34	Cloudy	Middle	3.0	18.00	18.00	18.00	7.81	7.81	7.81	31.06	31.06	31.06	76.4	76.9	76.8	6.00	6.05	6.03	2.38	2.32	2.32	4	3.50
	1:35	,	Middle	3.0	18.00	18.00		7.81	7.81		31.06	31.06		76.2	77.5		5.99	6.09		2.23	2.36		3	
23/1/19	3:45	Cloudy	Middle	2.5	16.50	16.50	16.50	8.38	8.38	8.38	31.77	31.77	31.77	85.2	85.7	86.5	6.87	6.91	6.98	2.82	2.84	2.93	3	3.00
	3:46	2.2007	Middle	2.5	16.50	16.50		8.38	8.38		31.77	31.77		87.9	87.3		7.09	7.04	2.30	3.01	3.03		3	
25/1/19	10:05	Fine	Middle	3.0	19.80	19.80	19.80	8.24	8.24	8.24	31.14	31.14	31.14	102.5	102.1	102.1	7.78	7.77	7.77	4.21	4.22	4.11	6	6.00
20, 1, 10	10:07		Middle	3.0	19.80	19.80		8.24	8.24	0.2 .	31.14	31.14		101.7	102.1		7.75	7.76		4.02	4.00		6	0.00

### Water Monitoring Result at P1 - HKCEC Phase I Mid-Ebb Tide

Date	Time	Weater Condition		ig Depth	Wat	er Temp	perature		pН			Salinit ppt	у	D	O Satur %	ation		DO ma/L			Turbid NTU		Suspend	led Solids
		Condition	r	n	Va	lue	Average	Va	lue	Average	Va	alue	Average	Va	lue	Average	Va		Average	Va	lue	Average	Value	Average
27/12/18	3:55	Cloudy	Middle	2.5	20.70	20.70	20.73	8.19	8.19	8.19	33.06	33.06	33.06	76.8	78.5	77.6	5.67	5.80	5.73	1.61	1.18	1.31	6	6.00
27/12/10	3:56	Cloudy	Middle	2.5	20.80	20.70	20.75	8.19	8.19	0.19	33.06	33.06	33.00	78.0	77.1	11.0	5.76	5.69	5.75	1.26	1.20	1.51	6	0.00
29/12/18	4:02	Cloudy	Middle	3.0	18.70	18.70	18.70	8.21	8.21	8.21	33.35	33.35	33.35	76.1	77.5	77.3	5.83	5.93	5.92	1.22	1.28	1.21	6	5.50
23/12/10	4:03	Cloudy	Middle	3.0	18.70	18.70	10.70	8.21	8.21	0.21	33.35	33.35	00.00	78.3	77.4	11.5	6.00	5.93	5.52	1.17	1.16	1.21	5	5.50
31/12/18	5:58	Cloudy	Middle	3.0	17.90	17.90	17.90	8.23	8.23	8.23	33.43	33.43	33.43	75.7	77.5	76.9	5.89	6.05	5.99	1.20	1.28	1.28	2	2.00
01/12/10	5:59	Cloudy	Middle	3.0	17.90	17.90	17.00	8.23	8.23	0.20	33.43	33.43	00.40	77.4	77.1	70.0	6.03	6.00	0.00	1.34	1.31	1.20	2	2.00
2/1/19	0:31	Cloudy	Middle	2.5	17.30	17.30	17.30	8.65	8.65	8.65	33.03	33.03	33.03	86.6	88.4	87.0	6.85	6.97	6.87	4.42	4.50	4.50	5	5.50
2/1/13	0:32	Cloudy	Middle	2.5	17.30	17.30	17.50	8.65	8.65	0.00	33.03	33.03	55.05	87.3	85.6	07.0	6.89	6.76	0.07	4.55	4.52	4.50	6	0.00
4/1/19	2:30	Cloudy	Middle	2.5	19.20	19.20	19.20	8.63	8.63	8.63	33.01	33.01	33.01	88.3	88.0	87.4	6.70	6.68	6.64	5.41	5.37	5.35	4	4.00
4/1/13	2:31	Cloudy	Middle	2.5	19.20	19.20	13.20	8.63	8.63	0.00	33.01	33.01	55.01	86.4	86.9	07.4	6.56	6.60	0.04	5.40	5.23	0.00	4	4.00
7/1/19	2:45	Cloudy	Middle	2.5	18.10	18.10	18.10	8.66	8.66	8.66	32.52	32.52	32.52	82.4	83.8	82.1	6.40	6.51	6.42	4.81	4.93	4.78	4	4.00
/////9	2:46	Cloudy	Middle	2.5	18.10	18.10	18.10	8.66	8.66	0.00	32.52	32.52	52.52	80.6	81.7	02.1	6.42	6.35	0.42	4.71	4.68	4.70	4	4.00
9/1/18	3:25	Cloudy	Middle	2.5	18.80	18.80	18.80	8.67	8.67	8.67	32.73	32.73	32.74	93.0	93.7	93.0	7.00	7.05	7.00	5.19	5.77	5.44	4	4.00
5/1/10	3:26	Cloudy	Middle	2.5	18.80	18.80	10.00	8.67	8.67	0.07	32.73	32.77	52.74	93.2	92.2	55.0	7.01	6.94	7.00	5.51	5.30	0.44	4	4.00
11/1/19	5:03	Cloudy	Middle	2.5	18.60	18.60	18.60	8.70	8.70	8.70	32.51	32.51	32.51	88.2	87.9	88.4	6.79	6.74	6.80	5.85	5.62	5.63	4	4.00
	5:04	Cloudy	Middle	2.5	18.60	18.60	10.00	8.70	8.70	0.70	32.51	32.51	02.01	89.0	88.4	66.4	6.85	6.81	0.00	5.54	5.50	0.00	4	4.00
14/1/19	3:45	Cloudy	Middle	3.0	18.70	18.70	18.70	8.62	8.62	8.62	32.28	32.28	32.28	91.2	93.4	92.5	7.02	7.19	7.12	2.23	2.02	2.08	<2	2.00
	3:46	Cloudy	Middle	3.0	18.70	18.70	10.70	8.62	8.62	0.02	32.28	32.28	02.20	93.0	92.2	02.0	7.15	7.10	7.12	1.99	2.07	2.00	2	2.00
16/1/19	21:41	Cloudy	Middle	3.0	17.50	17.50	17.50	8.71	8.71	8.71	32.04	32.04	32.04	89.8	89.9	90.2	7.08	7.09	7.10	2.58	2.12	2.26	4	3.50
10/1/10	21:42	Cloudy	Middle	3.0	17.50	17.50	17.00	8.71	8.71	0.71	32.04	32.04	02.04	89.7	91.5	00.2	7.06	7.17	7.10	2.09	2.26	2.20	3	0.00
18/1/19	21:39	Cloudy	Middle	3.0	19.10	19.10	19.10	7.84	7.84	7.84	32.16	32.16	32.16	88.0	89.2	89.2	6.61	6.72	6.71	2.81	2.55	2.55	5	4.50
10/1/10	21:04	Cloudy	Middle	3.0	19.10	19.10	13.10	7.84	7.84	7.04	32.16	32.16	52.10	89.1	90.4	00.2	6.72	6.79	0.71	2.42	2.40	2.55	4	4.00
21/1/19	1:06	Cloudy	Middle	3.0	17.90	17.90	17.90	7.78	7.78	7.78	30.17	30.17	30.17	69.9	70.7	70.7	5.50	5.59	5.59	2.78	2.75	2.74	3	3.00
21/1/13	1:07	Cioudy	Middle	3.0	17.90	17.90	17.30	7.78	7.78	1.10	30.17	30.17	30.17	71.3	71.0	10.1	5.64	5.61	5.55	2.72	2.70	2.14	3	3.00
23/1/19	3:13	Cloudy	Middle	2.5	16.40	16.40	16.40	8.35	8.35	8.35	31.22	31.22	31.22	91.6	91.5	90.7	7.43	7.42	7.36	3.29	3.42	3.27	3	3.00
20/1/10	3:14	Cidudy	Middle	2.5	16.40	16.40	10.40	8.35	8.35	0.00	31.22	31.22	01.22	91.0	88.6	50.7	7.38	7.19	7.00	3.21	3.15	0.21	3	0.00
25/1/19	9:45	Fine	Middle	3.0	18.80	18.80	18.85	7.53	7.53	7.54	30.74	30.74	30.74	99.4	99.4	98.9	7.69	7.69	7.65	3.01	3.00	2.96	8	8.50
20/1/10	9:47	1 110	Middle	3.0	18.90	18.90	10.05	7.55	7.55	7.54	30.74	30.74	50.74	98.2	98.5	50.5	7.59	7.64	7.00	2.91	2.92	2.50	9	0.00

Remarks: Single underline denotes exceedance over Action Level. Double underline denotes exceedance over Limit Level.

Water Monitoring Result at P3 - APA Mid-Ebb Tide

Date	Time	Weater Condition		ig Depth	Wat	er Temp °C	perature		pH -			Salinit ppt	у	D	O Satur %	ation		DO mg/L			Turbid NTL		Suspend	led Solids
		Oblidition	r	n	Va	lue	Average	Va	lue	Average	Va	alue	Average	Va	lue	Average	Va	lue	Average	Va	alue	Average	Value	Average
27/12/18	4:07	Cloudy	Middle	2.5	20.70	20.70	20.70	8.20	8.20	8.20	33.07	33.07	33.07	77.2	77.4	77.8	5.70	5.71	5.74	1.11	1.08	1.10	7	7.50
21/12/10	4:08	Cloudy	Middle	2.5	20.70	20.70	20.70	8.20	8.20	0.20	33.07	33.07	55.07	77.5	78.9	11.0	5.72	5.82	5.74	1.06	1.14	1.10	8	7.50
29/12/18	4:11	Cloudy	Middle	3.0	18.50	18.50	18.50	8.23	8.23	8.23	33.34	33.34	33.34	78.4	78.2	78.4	6.03	6.02	6.03	1.10	1.08	1.07	6	5.00
20/12/10	4:12	Cloudy	Middle	3.0	18.50	18.50	10.00	8.23	8.23	0.20	33.34	33.34	00.04	78.4	78.5	70.4	6.03	6.04	0.00	1.06	1.04	1.07	4	0.00
31/12/18	6:06	Cloudy	Middle	3.0	17.70	17.70	17.70	8.26	8.26	8.26	33.42	33.42	33.42	77.7	77.3	77.7	6.07	6.04	6.07	1.22	1.17	1.16	<2	3.00
01712/10	6:07	Cloudy	Middle	3.0	17.70	17.70	11.10	8.26	8.26	0.20	33.42	33.42	00.42	77.1	78.7		6.02	6.15	0.07	1.14	1.11	1.10	3	0.00
2/1/19	0:38	Cloudy	Middle	2.5	17.40	17.40	17.40	8.66	8.66	8.66	33.18	33.18	33.18	87.1	87.3	88.4	6.83	6.85	6.93	6.25	6.36	6.21	4	4.50
2,	0:39	cicady	Middle	2.5	17.40	17.40		8.66	8.66	0.00	33.18	33.18	00.10	89.7	89.4	00.1	7.04	7.01	0.00	6.07	6.15	0.121	5	
4/1/19	2:38	Cloudy	Middle	2.5	19.20	19.20	19.20	8.65	8.65	8.65	33.01	33.01	33.01	86.7	86.5	86.3	6.59	6.57	6.56	4.79	4.85	4.81	5	5.50
	2:39	cicady	Middle	2.5	19.20	19.20	.0.20	8.65	8.65	0.00	33.01	33.01	00.01	85.7	86.3	00.0	6.51	6.56	0.00	4.80	4.78		6	0.00
7/1/19	2:53	Cloudy	Middle	2.5	18.10	18.10	18.10	8.68	8.68	8.68	32.57	32.57	32.57	84.8	85.4	84.9	6.59	6.64	6.60	5.82	5.85	5.67	4	- 3.50
	2:54	cicady	Middle	2.5	18.10	18.10	10110	8.68	8.68	0.00	32.57	32.57	02.07	85.0	84.5	0 110	6.61	6.57	0.00	5.52	5.50	0.07	3	0.00
9/1/18	3:31	Cloudy	Middle	2.5	18.60	18.60	18.62	8.68	8.68	8.68	32.72	32.72	32.72	93.0	93.3	93.0	7.02	7.04	7.01	5.91	5.70	5.70	4	3.50
	3:32		Middle	2.5	18.60	18.68		8.68	8.68		32.72	32.72		92.8	92.7		7.00	6.99		5.62	5.57		3	
11/1/19	5:10	Cloudy	Middle	2.5	18.60	18.60	18.60	8.71	8.71	8.71	32.52	32.52	32.52	90.9	90.5	91.2	7.00	6.98	7.03	6.82	6.81	6.77	6	5.50
	5:11		Middle	2.5	18.60	18.60		8.71	8.71		32.52	32.52		91.8	91.6	-	7.07	7.06		6.75	6.70	-	5	
14/1/19	3:54	Cloudy	Middle	3.0	18.70	18.70	18.70	8.64	8.64	8.64	32.29	32.29	32.29	91.1	91.7	91.5	7.01	7.06	7.05	1.07	1.14	1.09	<2	2.00
	3:55		Middle	3.0	18.70	18.70		8.64	8.64		32.29	32.29		92.2	91.1		7.10	7.01		1.09	1.04		2	
16/1/19	21:47	Cloudy	Middle	3.0	17.70	17.70	17.70	8.72	8.72	8.72	32.03	32.03	32.03	90.6	91.7	91.9	7.11	7.20	7.22	2.77	2.71	2.72	6	5.50
	21:48		Middle	3.0	17.70	17.70		8.72	8.72		32.03	32.03		92.4	92.8		7.26	7.30		2.69	2.70		5	
18/1/19	21:47	Cloudy	Middle	3.0	19.00	19.00	19.00	7.86	7.86	7.86	32.17	32.17	32.17	91.6	93.7	92.1	6.89	7.05	6.93	2.72	2.82	2.77	4	4.00
	21:48	,	Middle	3.0	19.00	19.00		7.86	7.86		32.17	32.17	-	92.3	90.9		6.95	6.84		2.77	2.75		4	
21/1/19	1:12	Cloudy	Middle	3.0	17.90	17.90	17.90	7.77	7.77	7.77	30.64	30.64	30.64	74.7	75.0	75.0	5.90	5.91	5.92	2.60	2.41	2.34	4	4.00
	1:13	,	Middle	3.0	17.90	17.90		7.77	7.77		30.64	30.64		75.3	75.1		5.94	5.92		2.25	2.10	-	4	
23/1/19	3:19	Cloudy	Middle	2.5	16.30	16.30	16.30	8.33	8.33	8.33	31.20	31.20	31.20	89.1	87.6	88.7	7.24	7.12	7.21	3.26	3.34	3.30	3	3.00
	3:02	,	Middle	2.5	16.30	16.30		8.33	8.33		31.20	31.20		90.6	87.6		7.36	7.12		3.31	3.29		3	
25/1/19	9:50	Fine	Middle	3.0	18.60	18.60	18.55	8.16	8.16	8.16	31.10	31.10	31.10	101.4	101.6	101.2	7.79	7.81	7.74	3.92	3.90	3.89	8	- 7.50
	9:52	-	Middle	3.0	18.50	18.50		8.16	8.16		31.10	31.10		100.8	100.9	-	7.67	7.67		3.88	3.87		7	

Water Monitoring Result at P4 - SOC Mid-Ebb Tide

Date	Time	Weater Condition	Samplin	ng Depth	Wat	er Temp °C	erature		pН			Salinit ppt	y	C	O Satur	ation		DO ma/L			Turbid NTU		Suspend	ded Solids
		Oblidition	r	n	Va	lue	Average	Va	lue	Average	Va	alue	Average	Va	lue	Average	Va		Average	Va	lue	Average	Value	Average
27/12/18	4:14	Cloudy	Middle	2.5	20.70	20.70	20.70	8.20	8.20	8.20	33.06	33.06	33.06	75.9	77.9	76.5	5.61	5.75	5.65	1.13	1.19	1.17	7	6.50
27/12/10	4:15	Cloudy	Middle	2.5	20.70	20.70	20.70	8.20	8.20	0.20	33.06	33.06	33.00	75.5	76.5	70.5	5.58	5.65	5.05	1.12	1.22	1.17	6	0.50
29/12/18	4:18	Cloudy	Middle	3.0	18.70	18.70	18.70	8.25	8.25	8.25	33.34	33.34	33.34	72.7	75.2	74.5	5.58	5.77	5.72	1.02	1.07	1.08	6	7.00
20/12/10	4:19	Cloudy	Middle	3.0	18.70	18.70	10.70	8.25	8.25	0.20	33.34	33.34	00.04	75.1	74.9	14.0	5.77	5.75	0.72	1.13	1.11	1.00	8	7.00
31/12/18	6:11	Cloudy	Middle	3.0	17.60	17.60	17.60	8.28	8.28	8.28	33.41	33.41	33.41	79.1	79.5	79.4	6.18	6.22	6.21	1.33	1.42	1.44	3	2.50
01/12/10	6:12	Cloudy	Middle	3.0	17.60	17.60	17.00	8.28	8.28	0.20	33.41	33.41	00.41	79.1	80.0	70.4	6.19	6.25	0.21	1.49	1.51	1.44	2	2.00
2/1/19	0:44	Cloudy	Middle	2.5	17.60	17.60	17.60	8.67	8.67	8.67	33.13	33.13	33.13	86.4	86.7	87.5	6.76	6.79	6.85	5.22	5.40	5.22	6	5.50
2,1,10	0:45	cicady	Middle	2.5	17.60	17.60		8.67	8.67	0.07	33.13	33.13	00.10	88.6	88.2	01.0	6.93	6.90	0.00	5.09	5.18	0.22	5	0.00
4/1/19	2:46	Cloudy	Middle	2.5	19.20	19.20	19.20	8.66	8.66	8.66	32.99	32.98	32.98	87.2	86.9	87.4	6.62	6.60	6.64	4.65	4.60	4.60	5	5.00
	2:47	Cloudy	Middle	2.5	19.20	19.20	10.20	8.66	8.66	0.00	32.98	32.98	02.00	87.5	87.8	07.4	6.65	6.68	0.04	4.58	4.55	4.00	5	0.00
7/1/19	3:02	Cloudy	Middle	2.5	18.10	18.10	18.10	8.68	8.68	8.68	32.58	32.58	32.58	85.2	85.5	84.9	6.62	6.65	6.60	5.74	5.70	5.74	4	3.50
	3:03	Cloudy	Middle	2.5	18.10	18.10	10.10	8.68	8.68	0.00	32.58	32.58	02.00	84.8	84.0	04.0	6.59	6.53	0.00	5.80	5.72	0.74	3	0.00
9/1/18	3:40	Cloudy	Middle	2.5	18.70	18.70	18.70	8.68	8.68	8.68	32.71	32.71	32.71	85.5	91.4	88.6	6.44	6.89	6.67	6.87	6.72	6.73	4	4.00
	3:41	cicady	Middle	2.5	18.70	18.70		8.68	8.68	0.00	32.71	32.71	02 1	89.2	88.3	00.0	6.71	6.65	0.07	6.69	6.62	0.10	4	
11/1/19	5:18	Cloudy	Middle	2.5	18.60	18.60	18.60	8.71	8.71	8.71	32.51	32.51	32.51	92.3	93.0	92.0	7.11	7.16	7.09	6.01	5.98	5.94	5	5.50
	5:19		Middle	2.5	18.60	18.60		8.71	8.71		32.51	32.51		92.0	90.8		7.09	7.00		5.92	5.84		6	
14/1/19	4:07	Cloudy	Middle	3.0	18.70	18.70	18.70	8.64	8.64	8.64	32.28	32.28	32.28	91.4	92.7	92.6	7.04	7.13	7.13	1.14	1.18	1.15	<2	<2
	4:08	,	Middle	3.0	18.70	18.70		8.64	8.64		32.28	32.28		93.4	92.7		7.19	7.14		1.20	1.09		<2	
16/1/19	21:56	Cloudy	Middle	3.0	17.60	17.60	17.60	8.73	8.73	8.73	32.05	32.05	32.05	89.5	89.8	90.3	7.05	7.08	7.12	2.40	2.38	2.16	6	5.50
	21:57		Middle	3.0	17.60	17.60		8.73	8.73		32.05	32.05		90.6	91.2		7.14	7.19		2.50	1.37		5	
18/1/19	21:53	Cloudy	Middle	3.0	18.90	18.90	18.90	7.87	7.87	7.87	32.17	32.17	32.17	88.9	89.5	90.4	6.70	6.75	6.80	1.86	1.82	1.76	5	5.00
	21:54	cicady	Middle	3.0	18.90	18.90	10.00	7.87	7.87		32.17	32.17	02	91.5	91.6		6.85	6.90	0.00	1.66	1.69		5	0.00
21/1/19	1:17	Cloudy	Middle	3.0	17.80	17.80	17.80	7.78	7.78	7.78	30.66	30.66	30.66	70.4	71.8	70.8	5.57	5.68	5.60	1.95	1.73	1.79	5	5.50
	1:18	0.0009	Middle	3.0	17.80	17.80		7.78	7.78		30.66	30.66	00.00	70.6	70.5		5.58	5.58	0.00	1.67	1.79		6	0.00
23/1/19	3:27	Cloudy	Middle	2.5	16.40	16.40	16.40	8.32	8.32	8.32	31.20	31.20	31.20	93.0	92.1	92.5	7.54	7.46	7.49	3.89	3.92	3.87	3	3.00
20,1710	3:28	0.0009	Middle	1.5	16.40	16.40		8.32	8.32	0.0L	31.20	31.20	020	92.2	92.6	02.0	7.47	7.50		3.85	3.80	0.07	3	0.00
25/1/19	9:55	Fine	Middle	3.0	19.70	19.70	19.75	8.19	8.19	8.20	31.15	31.15	31.15	99.2	100.2	99.7	7.54	7.61	7.58	3.68	3.66	3.66	8	8.00
20/11/0	9:57		Middle	3.0	19.80	19.80		8.20	8.20	5	31.15	31.15	00	99.5	99.9		7.56	7.59		3.64	3.64	0.00	8	0.00

### Water Monitoring Result at P5 - WCT / RT / IT Mid-Ebb Tide

Date	Time	Weater Condition		ng Depth	Wat	er Temp °C	erature		рH			Salinit ppt	y.	C	O Satur	ation		DO ma/L			Turbid NTU		Suspend	led Solids
		Condition	r	n	Va	lue	Average	Va	lue	Average	Va	alue	Average	Va	lue	Average	Va	lue	Average	Va	lue	Average	Value	Average
27/12/18	4:20	Cloudy	Middle	2.5	20.70	20.70	20.70	8.21	8.20	8.21	33.05	33.05	33.05	77.7	77.6	77.2	5.73	5.73	5.70	1.71	1.39	1.52	5	5.00
27/12/10	4:21	Cloudy	Middle	2.5	20.70	20.70	20.70	8.21	8.21	0.21	33.05	33.05	00.00	76.8	76.5	11.2	5.67	5.65	5.70	1.67	1.30	1.02	5	3.00
29/12/18	4:24	Cloudy	Middle	3.0	18.50	18.50	18.50	8.26	8.26	8.26	33.35	33.35	33.35	76.5	76.3	76.5	5.87	5.85	5.88	1.26	1.15	1.20	6	6.00
23/12/10	4:25	Cloudy	Middle	3.0	18.50	18.50	10.50	8.26	8.26	0.20	33.35	33.35	00.00	77.1	76.1	70.5	5.92	5.86	5.00	1.20	1.18	1.20	6	0.00
31/12/18	6:16	Cloudy	Middle	3.0	17.80	17.80	17.80	8.29	8.29	8.29	33.31	33.31	33.27	73.3	75.8	75.0	5.72	5.92	5.86	1.40	1.36	1.37	2	2.00
01/12/10	6:17	Cloudy	Middle	3.0	17.80	17.80	17.00	8.29	8.29	0.20	33.13	33.31	00.27	75.9	75.1	70.0	5.93	5.87	0.00	1.33	1.38	1.07	2	2.00
2/1/19	0:53	Cloudy	Middle	2.5	17.60	17.60	17.60	8.69	8.69	8.69	33.06	33.06	33.06	81.2	82.8	83.8	6.35	6.48	6.56	4.42	4.46	4.50	4	4.50
2,1,10	0:54	cicady	Middle	2.5	17.60	17.60	17.00	8.69	8.69	0.00	33.06	33.06	00.00	85.7	85.5	00.0	6.71	6.69	0.00	4.53	4.60		5	
4/1/19	2:55	Cloudy	Middle	2.5	19.30	19.30	19.30	8.67	8.67	8.67	33.02	33.02	33.02	87.8	88.6	88.2	6.66	6.72	6.69	5.57	5.53	5.55	5	5.00
-11/10	2:56	Cloudy	Middle	2.5	19.30	19.30	10.00	8.67	8.67	0.07	33.02	33.02	00.02	88.4	88.0	00.2	6.71	6.67	0.00	5.59	5.51	0.00	5	0.00
7/1/19	3:10	Cloudy	Middle	2.5	18.20	18.20	18.20	8.68	8.68	28.66	32.49	32.49	32.49	85.5	84.5	83.9	6.65	5.57	6.27	6.13	6.09	6.07	3	3.00
	3:11	Cloudy	Middle	2.5	18.20	18.20	10.20	8.60	88.68	20.00	32.49	32.49	02.40	83.1	82.5	66.5	6.46	6.41	0.27	6.03	6.01	0.07	3	0.00
9/1/18	3:47	Cloudy	Middle	2.5	18.10	18.10	18.10	8.63	8.63	8.63	32.73	32.73	32.73	87.0	85.9	86.7	6.64	6.56	6.62	6.09	6.44	6.37	5	5.00
6, 1, 10	3:48	cicady	Middle	2.5	18.10	18.10	10.110	8.63	8.63	0.00	32.73	32.73	02.70	86.9	86.8		6.64	6.62	0.02	6.42	6.51	0.07	5	0.00
11/1/19	5:24	Cloudy	Middle	2.5	18.50	18.50	18.50	8.71	8.71	8.71	32.51	32.51	32.51	91.0	91.1	91.3	7.01	7.02	7.04	7.37	7.40	7.35	3	3.00
	5:25		Middle	2.5	18.50	18.50		8.71	8.71		32.51	32.51		91.7	91.5		7.07	7.05		7.33	7.30		3	
14/1/19	4:11	Cloudy	Middle	3.0	18.80	18.80	18.80	8.65	8.65	8.65	32.22	32.22	32.22	91.1	91.6	91.6	7.01	7.04	7.05	1.05	1.18	1.11	<2	<2
	4:12		Middle	3.0	18.80	18.80		8.65	8.65		32.22	32.22		92.4	91.3		7.11	7.02		1.17	1.04		<2	
16/1/19	22:03	Cloudy	Middle	3.0	17.70	17.70	17.70	8.74	8.74	8.74	32.05	32.05	32.05	90.9	89.6	90.4	7.17	7.07	7.12	2.09	2.27	2.23	5	4.50
	22:04	,	Middle	3.0	17.70	17.70		8.74	8.74	-	32.05	32.05		89.7	91.5		7.06	7.19		2.25	2.31		4	
18/1/19	21:59	Cloudy	Middle	3.0	18.90	18.90	18.90	7.88	7.88	7.88	32.17	32.17	32.17	90.2	89.9	90.6	6.79	6.77	6.83	2.46	2.28	2.31	4	4.00
	22:00		Middle	3.0	18.90	18.90		7.88	7.88		32.17	32.17		90.6	91.7		6.84	6.91		2.25	2.23		4	
21/1/19	1:24	Cloudy	Middle	3.0	18.00	18.00	18.00	7.79	7.79	7.79	31.06	31.06	31.06	77.6	76.6	76.2	6.10	6.03	5.99	1.64	1.81	1.81	2	3.00
	1:25		Middle	3.0	18.00	18.00		7.79	7.79		31.06	31.06		75.9	74.7		5.97	5.87	2.30	1.91	1.87		4	
23/1/19	3:36	Cloudy	Middle	2.5	16.80	16.80	16.80	8.32	8.32	8.32	31.21	31.21	31.21	88.3	88.0	89.2	7.11	7.08	7.19	3.01	3.21	3.20	3	3.50
	3:37		Middle	2.5	16.80	16.80		8.32	8.32		31.21	31.21		89.8	90.8		7.23	7.32		3.27	3.29		4	
25/1/19	10:00	Fine	Middle	3.0	19.80	19.80	19.80	8.23	8.23	8.23	31.09	31.09	31.12	100.1	100.2	100.0	7.60	7.60	7.59	4.00	4.02	4.04	9	8.50
	10:02		Middle	3.0	19.80	19.80		8.23	8.23		31.15	31.15		100.0	99.8		7.59	7.57		4.04	4.08		8	



#### Water Monitoring Result at RW21-P789 - GEC / CRB / SHK Mid-Ebb Tide


Date	Time	Weater Condition		ig Depth	Wat	er Temp °C	erature		pН			Salini ppt	ty	[	DO Satur %	ration		DO ma/L			Turbid NTU		Suspend	led Solids
		Contailion	r	n	Va	lue	Average	Va	lue	Average	Va	alue	Average	Va	alue	Average	Va	lue	Average	Va	lue	Average	Value	Average
27/12/18	4:47	Cloudy	Middle	3.5	20.70	20.70	20.70	8.12	8.12	8.12	32.65	32.65	32.65	70.8	71.3	71.0	5.24	5.28	5.25	1.37	1.39	1.41	<2	<2
	4:48	,	Middle	3.5	20.70	20.70		8.12	8.12		32.65	32.65		71.0	70.7		5.25	5.24		1.46	1.41		<2	
29/12/18	5:52	Cloudy	Middle	3.5	18.60	18.60	18.60	8.27	8.27	8.27	31.91	31.91	31.91	68.6	69.7	69.5	5.33	5.41	5.40	1.15	1.13	1.12	3	3.00
	5:53		Middle	3.5	18.60	18.60		8.27	8.27		31.91	31.91		69.9	69.6		5.43	5.41		1.10	1.09		3	
31/12/18	5:25	Cloudy	Middle	4.0	16.40	16.40	16.40	8.07	8.07	8.07	32.49	32.49	32.49	74.3	73.9	74.3	5.98	5.95	5.98	1.26	1.31	1.33	<2	<2
	5:26		Middle	4.0	16.40	16.40		8.07	8.07		32.49	32.49		75.0	74.1		6.04	5.96		1.34	1.39		<2	
2/1/19	22:10	Cloudy	Middle	3.5	17.60	17.60	17.60	8.39	8.39	8.39	32.12	32.12	32.12	78.2	79.9	78.5	6.12	6.29	6.16	3.56	3.47	3.49	5	4.50
	22:11		Middle	4.0	17.60	17.60		8.39	8.39		32.12	32.12		78.4	77.3		6.18	6.05		3.50	3.44		4	
4/1/19	23:15	Cloudy	Middle	4.0	19.30	19.30	19.30	8.48	8.48	8.48	32.68	32.68	32.68	87.0	88.2	87.1	6.63	6.71	6.63	4.71	4.69	4.58	3	2.50
	23:16		Middle	4.0	19.30	19.30		8.48	8.48		32.68	32.68		87.0	86.3		6.63	6.56		4.44	4.49		2	
7/1/19	3:43	Cloudy	Middle	3.5	18.30	18.30	18.30	8.53	8.53	8.53	32.04	32.04	32.04	77.8	79.5	79.4	6.05	6.18	6.17	4.43	4.33	4.36	5	4.50
	3:44		Middle	3.5	18.30	18.30		8.53	8.53		32.04	32.04		79.9	80.3		6.20	6.24		4.35	4.32		4	
9/1/18	4:30	Cloudy	Middle	3.5	18.30	18.30	18.30	8.43	8.43	8.43	30.45	30.45	30.45	86.0	85.6	85.7	6.62	6.59	6.60	4.12	4.26	4.19	<2	<2
	4:31	-	Middle	3.5	18.30	18.30		8.43	8.43		30.45	30.45		86.3	85.0		6.64	6.54		4.22	4.14		<2	
11/1/19	5:50	Cloudy	Middle	3.5	18.60	18.60	18.60	8.65	8.65	8.65	31.71	31.71	31.71	90.8	92.2	91.7	7.03	7.13	7.10	5.52	6.04	5.69	3	3.50
	5:51		Middle	3.5	18.60	18.60		8.65	8.65		31.71	31.71		92.5	91.3		7.16	7.06		5.58	5.63		4	
14/1/19	5:12	Cloudy	Middle	3.5	18.80	18.80	18.80	8.49	8.49	8.49	32.20	32.20	24.71	91.7	92.6	92.1	7.05	7.12	7.08	1.05	1.29	1.15	<2	<2
	5:13		Middle	3.5	18.80	18.80		8.50	8.49		32.23	2.20		92.2	91.7		7.09	7.05		1.08	1.19		<2	
16/1/19	22:35	Cloudy	Middle	3.5	17.90	17.90	17.90	8.61	8.61	8.61	30.12	30.12	30.12	82.7	84.0	83.3	6.54	6.65	6.59	2.65	2.41	2.47	5	5.50
	22:36		Middle	3.5	17.90	17.90		8.61	8.61		30.12	30.11		82.8	83.8		6.55	6.63		2.38	2.44		6	
18/1/19	23:03	Cloudy	Middle	3.5	19.00	19.00	19.00	7.83	7.83	7.83	32.06	32.06	32.06	83.7	86.4	86.4	6.30	6.50	6.50	1.33	1.21	1.24	3	3.50
	23:04	-	Middle	3.5	19.00	19.00		7.83	7.83		32.06	32.06		87.9	87.4		6.61	6.57		1.18	1.24		4	
21/1/19	2:20	Cloudy	Middle	3.5	17.90	17.90	17.90	7.76	7.76	7.76	30.90	30.90	30.90	76.0	76.6	76.4	5.99	6.03	6.02	2.09	2.02	1.96	3	3.50
	2:21	-	Middle	3.5	17.90	17.90		7.76	7.76		30.90	30.90		76.7	76.3		6.04	6.01		1.87	1.85		4	
23/1/19	4:10	Cloudy	Middle	3.5	16.60	16.60	16.60	8.07	8.07	8.07	30.33	30.33	30.33	79.0	79.6	79.7	6.42	6.48	6.48	1.91	1.93	1.90	4	4.00
	4:11	-	Middle	3.5	16.60	16.60		8.07	8.07		30.33	30.33		80.4	79.7		6.54	6.49		1.96	1.80		4	
25/1/19	10:20	Fine	Middle	4.0	18.60	18.60	18.60	7.81	7.81	7.84	30.96	30.96	30.98	92.0	92.0	91.9	7.16	7.16	7.14	4.79	4.80	4.81	10	9.00
	10:22		Middle	4.0	18.60	18.60		7.87	7.87		30.99	30.99		91.8	91.9		7.11	7.14		4.81	4.82		8	





### Water Monitoring Result at WSD19 - Sheung Wan Mid-Ebb Tide


Date	Time	Weater Condition		ig Depth	Wat	er Temp °C	erature		pH -			Salinit ppt	у	D	O Satur %	ation		DO mg/L			Turbid NTU		Suspend	led Solids a/L
			n	n	Va	lue	Average	Va	lue	Average	Va		Average	Va	lue	Average	Va		Average	Va	alue	Average	Value	Average
27/12/18	2:54	Cloudy	Middle	4.0	20.50	20.50	20.50	8.06	8.07	8.07	32.98	32.98	32.98	71.8	73.8	72.8	5.33	5.48	5.41	1.20	1.24	1.22	5	5.00
	2:55	cicady	Middle	4.0	20.50	20.50	20.00	8.07	8.07	0.07	32.98	32.98	02.00	73.1	72.5	72.0	5.43	5.38	0.11	1.18	1.26		5	0.00
29/12/18	2:45	Cloudy	Middle	4.0	18.10	18.10	18.10	8.04	8.04	8.04	32.70	32.70	32.70	74.6	76.4	76.2	5.60	5.95	5.88	1.63	1.33	1.37	5	5.50
	2:46	,	Middle	4.0	18.10	18.10		8.04	8.04		32.70	32.70		76.2	77.4		5.93	6.03		1.29	1.24		6	
31/12/18	5:37	Cloudy	Middle	4.0	16.50	16.50	16.50	8.09	8.10	8.10	32.71	32.71	32.71	77.3	77.5	76.9	6.22	6.23	6.19	1.73	1.94	1.88	5	5.00
	5:38		Middle	4.0	16.50	16.50		8.10	8.10		32.71	32.71	-	77.2	75.7		6.21	6.10		2.03	1.83		5	
2/1/19	23:07	Cloudy	Middle	3.5	18.00	18.00	18.00	8.13	8.13	8.13	32.12	32.12	32.12	82.2	85.3	84.1	6.44	6.69	6.60	5.31	5.22	5.26	5	5.50
	23:08		Middle	3.5	18.00	18.00		8.13	8.13		32.12	32.12	-	85.8	83.1	-	6.73	6.52		5.28	5.24		6	
4/1/19	0:35	Cloudy	Middle	4.0	19.20	19.20	19.20	8.29	8.29	8.29	32.31	32.31	32.31	86.4	87.2	86.6	6.58	6.64	6.59	7.19	7.04	7.05	5	5.00
	0:36	,	Middle	4.0	19.20	19.20		8.29	8.29		32.31	32.31		87.0	85.7		6.62	6.53		7.00	6.98		5	
7/1/19	0:30	Cloudy	Middle	4.0	18.10	18.10	18.10	8.39	8.39	8.39	31.94	31.94	31.95	87.6	86.6	87.1	6.84	6.76	6.81	5.56	5.52	5.43	4	4.50
	0:31	cicady	Middle	4.0	18.10	18.10		8.39	8.39	0.00	31.96	31.96	01.00	87.1	87.2	0	6.83	6.81	0.01	5.44	5.19	0.10	5	
9/1/18	1:30	Cloudy	Middle	4.0	18.40	18.40	18.40	8.34	8.34	8.34	32.23	32.23	32.23	88.4	89.1	88.8	6.72	6.77	6.75	5.62	5.60	5.62	3	3.50
	1:31		Middle	4.0	18.40	18.40		8.34	8.34		32.23	32.23		88.7	89.0		6.74	6.76		5.59	5.65		4	
11/1/19	2:20	Cloudy	Middle	4.0	18.90	18.90	18.90	8.60	8.60	8.60	32.34	32.34	32.34	91.4	93.0	91.7	7.01	7.13	7.03	7.96	7.88	7.87	6	6.50
	2:21	,	Middle	4.0	18.90	18.90		8.60	8.60		32.34	32.34		91.1	91.2	-	6.98	6.99		7.85	7.80	-	7	
14/1/19	2:15	Cloudy	Middle	4.0	18.90	18.90	18.90	8.37	8.37	8.37	31.90	31.90	31.90	89.3	92.5	91.6	6.88	7.13	7.06	3.40	3.36	3.30	<2	2.00
	2:16		Middle	4.0	18.90	18.90		8.37	8.37		31.90	31.90		93.3	91.1		7.19	7.02		3.28	3.16		2	
16/1/19	20:32	Cloudy	Middle	4.0	18.10	18.10	18.10	8.56	8.56	8.56	32.18	32.18	32.18	88.3	87.9	88.9	6.87	6.84	6.87	2.93	2.75	2.77	10	9.50
	20:33		Middle	4.0	18.10	18.10		8.56	8.56		32.18	32.18		89.0	90.5		6.72	7.04		2.72	2.69		9	
18/1/19	20:45	Cloudy	Middle	4.0	18.60	18.60	18.60	7.95	7.95	7.95	32.19	32.19	32.19	85.2	86.3	87.8	6.41	6.50	6.61	2.62	2.13	2.29	5	5.00
	20:46	,	Middle	4.0	18.60	18.60		7.95	7.95		32.19	32.19	-	89.7	89.8	-	6.75	6.76		2.23	2.17		5	
21/1/19	23:33	Cloudy	Middle	4.0	18.00	18.00	18.00	7.72	7.72	7.72	31.87	31.87	31.87	84.5	83.8	83.8	6.61	6.55	6.55	2.88	2.86	2.82	6	5.50
	23:34	,	Middle	4.0	18.00	18.00		7.72	7.72		31.87	31.87		83.5	83.4		6.53	6.50		2.75	2.78	-	5	
23/1/19	1:15	Cloudy	Middle	4.0	15.90	15.90	15.90	7.76	7.76	7.76	31.04	31.04	31.04	80.4	82.2	83.2	6.59	6.74	6.82	2.42	3.09	2.93	3	2.50
-/	1:16		Middle	4.0	15.90	15.90		7.76	7.76		31.04	31.04		86.7	83.5		7.11	6.85		3.12	3.09		2	
25/1/19	11:00	Fine	Middle	4.0	19.00	19.00	19.05	7.97	7.97	7.98	31.12	31.12	31.12	93.1	93.7	92.9	7.17	7.18	7.14	3.06	3.08	3.06	11	10.50
	11:02		Middle	4.0	19.10	19.10		7.99	7.99		31.11	31.11		92.1	92.6		7.08	7.12		3.08	3.02		10	

Graphic Presentation of Water Quality Result of WSD19 - Sheung Wan

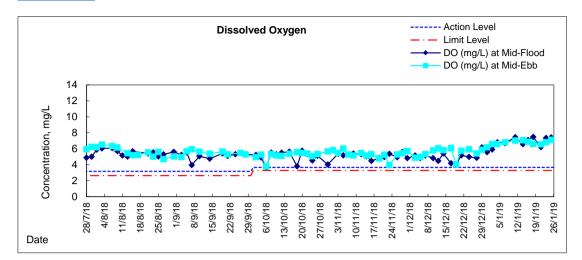


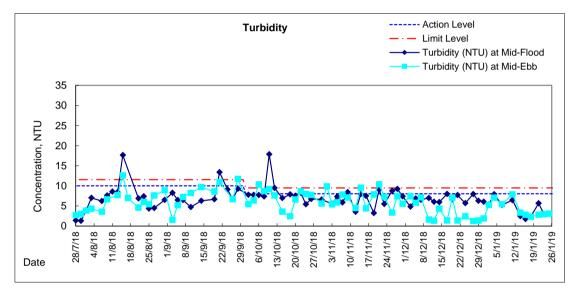


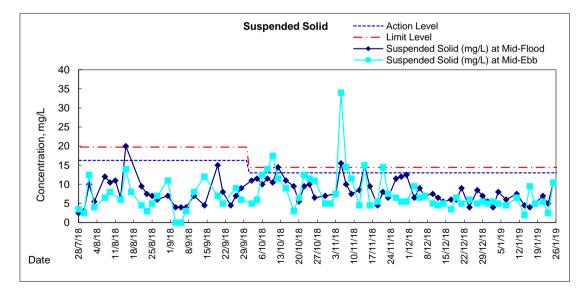


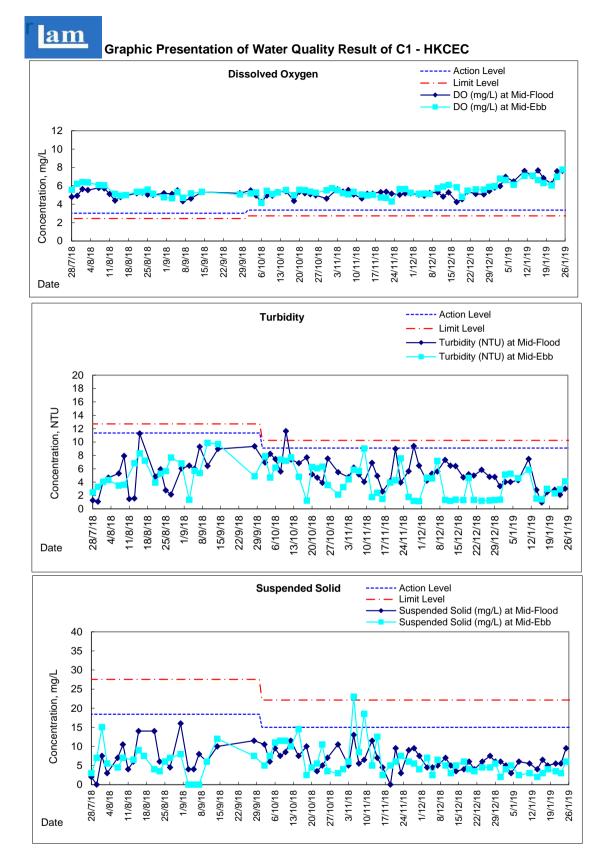

Graphic Presentation of Water Quality Result of P1 - HKCEC Phase I

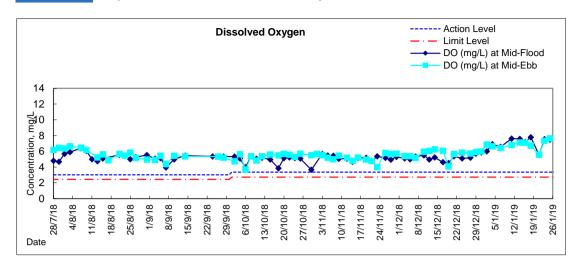


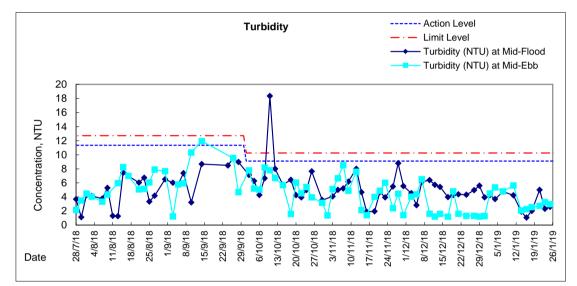


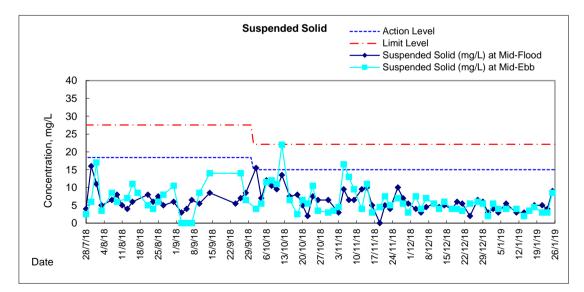





Graphic Presentation of Water Quality Result of P3 - APA

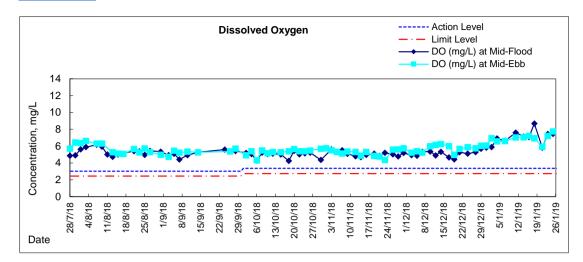


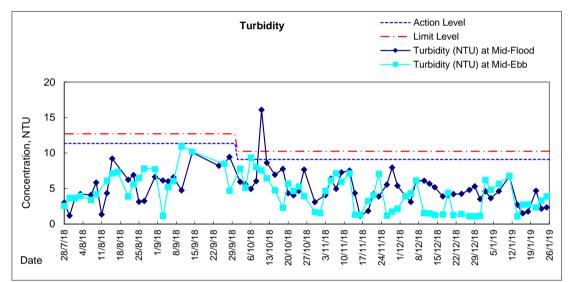


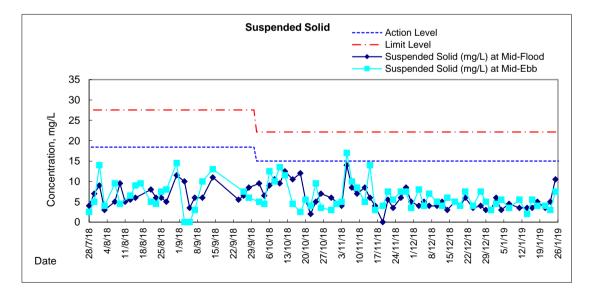


Graphic Presentation of Water Quality Result of P5 - WCT / RT / IT

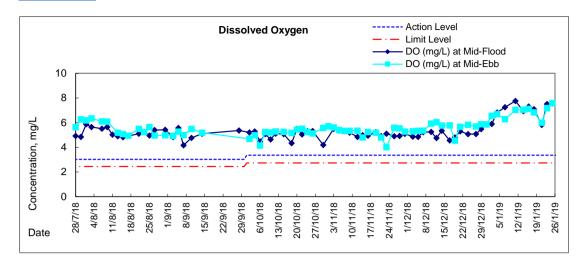


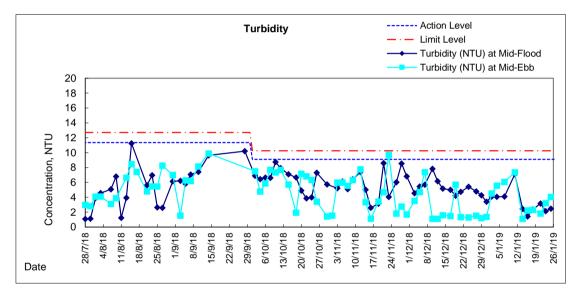


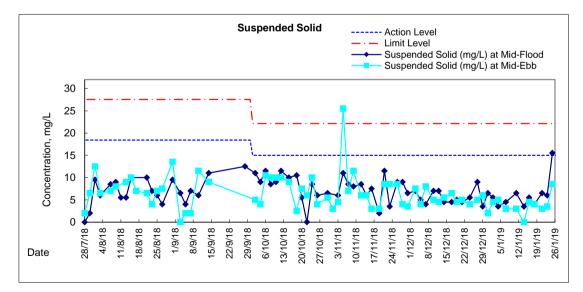



Graphic Presentation of Water Quality Result of P4 - SOC

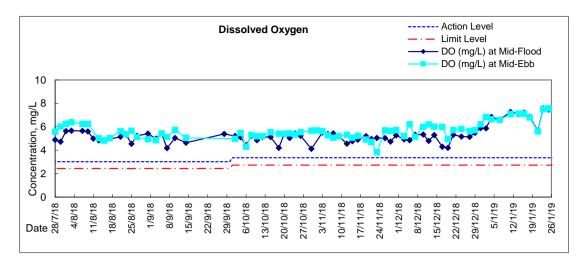


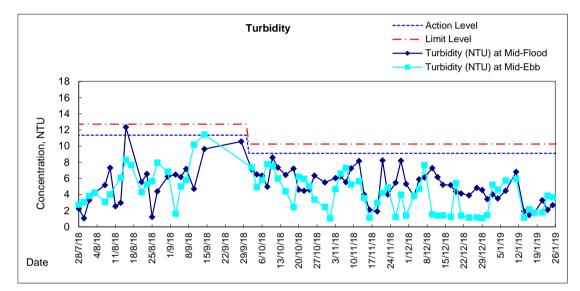

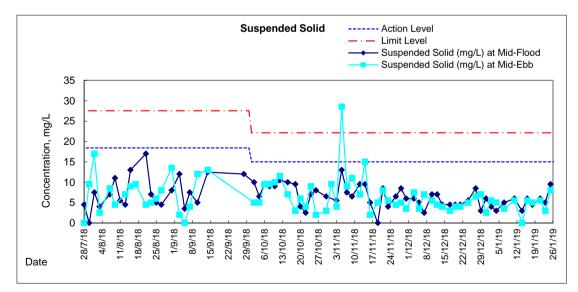

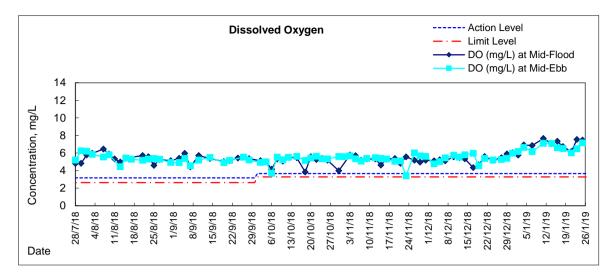

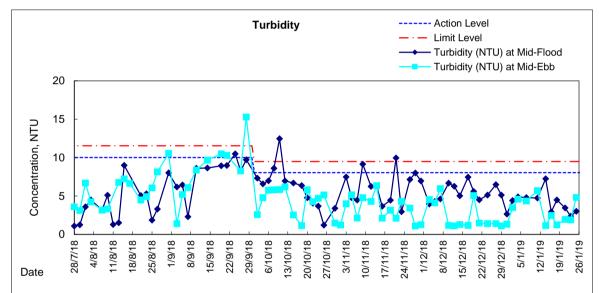

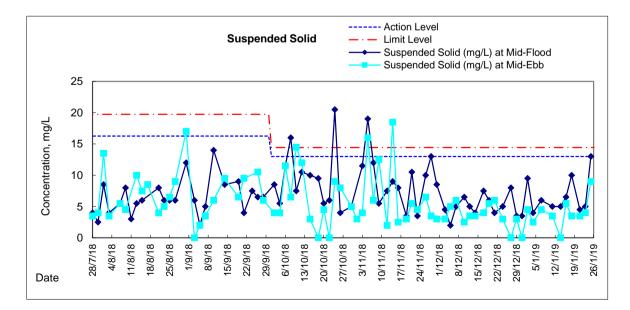



Appendix 6.1

**Event Action Plans** 



### **Event/Action Plan for Construction Noise**

EVENT		A	CTION	
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	<ol> <li>Notify ER, IEC and Contractor;</li> <li>Carry out investigation;</li> <li>Report the results of investigation to the IEC, ER and Contractor;</li> <li>Discuss with the IEC and Contractor on remedial measures required;</li> <li>Increase monitoring frequency to check mitigation effectiveness.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Review the investigation results submitted by the ET;</li> <li>Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Supervise the implementation of remedial measures.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Submit noise mitigation proposals to IEC and ER;</li> <li>Implement noise mitigation proposals.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit Level being exceeded	<ol> <li>Inform IEC, ER, Contractor and EPD;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency;</li> <li>4. Identify source and investigate the cause of exceedance;</li> <li>5. Carry out analysis of Contractor's working procedures;</li> <li>6. Discuss with the IEC, Contractor and ER on remedial measures required;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>If exceedance stops, cease additional monitoring.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Supervise the implementation of remedial measures;</li> <li>If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC and ER within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Submit further proposal if problem still not under control;</li> <li>Stop the relevant portion of works as instructed by the ER until the exceedance is abated.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>



### Event / Action Plan for Construction Air Quality

EVENT	ACTION				
EVENT	ET	IEC	ER	CONTRACTOR	
ACTION LEVEL					
1. Exceedance for one sample	<ol> <li>Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>Inform IEC and ER;</li> <li>Repeat measurement to confirm finding;</li> <li>Increase monitoring frequency to daily.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	Notify Contractor.     (The above actions should be taken within 2     working days after the exceedance is identified)	<ol> <li>Rectify any unacceptable practice;</li> <li>Amend working methods if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	
2. Exceedance for two or more consecutive samples	<ol> <li>Identify source;</li> <li>Inform IEC and ER;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Discuss with IEC and Contractor on remedial actions required;</li> <li>If exceedance continues, arrange meeting with IEC and ER;</li> <li>If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with ET and Contractor on possible remedial measures;</li> <li>Advise the ET on the effectiveness of the proposed remedial measures;</li> <li>Supervise Implementation of remedial measures.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>Ensure remedial measures properly implemented.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Submit proposals for remedial to ER within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	
LIMIT LEVEL					
1. Exceedance for one sample	<ol> <li>Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>Inform ER, Contractor and EPD;</li> <li>Repeat measurement to confirm finding;</li> <li>Increase monitoring frequency to daily;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with ET and Contractor on possible remedial measures;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>Supervise implementation of remedial measures.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>Ensure remedial measures properly implemented.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	
2. Exceedance for two or more consecutive samples	<ol> <li>Notify IEC, ER, Contractor and EPD;</li> <li>Identify source;</li> <li>Repeat measurement to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>Supervise the implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Ensure remedial measures properly implemented;</li> <li>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Resubmit proposals if problem still not under control;</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	



### Event and Action Plan for Marine Water Quality

EVENT	ACTION				
	ET	IEC	ER	CONTRACTOR	
Action level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	
Action level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next working day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Limit level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3working days; Implement the agreed mitigation measures; As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities. (The above actions should be taken within 1 working day after the exceedance is identified)



## Event and Action Plan for Odour Patrol

Event		ACTION
	Person-in-charge of Odour Monitoring	Implementation Agent Identified by CEDD
Action Level		
Exceedance of Action Level	<ol> <li>Identify source/reason of exceedance;</li> <li>Repeat odour patrol to confirm finding.</li> </ol>	<ol> <li>Carry out investigation to identify the source/reason of exceedance;</li> <li>Rectify any unacceptable practice</li> <li>Implement more mitigation measures if necessary;</li> <li>Inform EPD or MD if exceedance is considered to be caused by expedient connections or floating debris.</li> </ol>
Limit Level		
Exceedance of Limit Level	<ol> <li>Identify source / reason of exceedance;</li> <li>Repeat odour patrol to confirm findings;</li> <li>Increase odour patrol frequency;</li> <li>If exceedance stops, cease additional odour patrol.</li> </ol>	<ol> <li>Carry out investigation to identify the source/reason of exceedance. Investigation shall be completed within 2 weeks;</li> <li>Rectify any unacceptable practice;</li> <li>Formulate remedial actions;</li> <li>Ensure remedial actions properly implemented;</li> <li>If exceedance continues, consider what more/enhanced mitigation measures shall be implemented;</li> <li>Inform EPD or MD if exceedance is considered to be caused by expedient connections or floating debris.</li> </ol>



Appendix 6.2

Summary for Notification of Exceedance



Ref. No.	Date	Time	Location	Construction Noise Level, dB(A)	Parameter	Action Level	Limit Level dB(A)	Follow-up action	
X_19N001	18-Jan-19	10:50	M6 - HK Baptist Church Henrietta Secondary School	68	Leq(30min)	when one documented complaint was received.	65	Possible reason:	Traffic nearby was observed during monitoring and was considered as the major noise contribution.
								Action taken / to be taken:	A repeat measurement was conducted to confirm result and reviewed the trend of previous noise monitoring and Contractor's working procedure.
								Remarks / Other Obs:	No construction works was conducted under HY/2009/19 around the monitoring location and nearby traffic noise was observed as major noise source during monitoring. As such, the exceedance was considered as non-Project related.



Ref. No.	Date	Time	Location	Construction Noise Level, dB(A)	Parameter	Action Level	Limit Level dB(A)	Follow-up action	
X_19N002	25-Jan-19	11:20	M6 - HK Baptist Church Henrietta Secondary School	69	Leq(30min)	when one documented complaint was received.	65	Possible reason:	Traffic nearby was observed during monitoring and was considered as the major noise contribution.
								Action taken / to be taken:	A repeat measurement was conducted to confirm result and reviewed the trend of previous noise monitoring and Contractor's working procedure.
								Remarks / Other Obs:	No construction works was conducted under HY/2009/19 around the monitoring location and nearby traffic noise was observed as major noise source during monitoring. As such, the exceedance was considered as non-Project related.



Contract No. HK/2015/01 Wanchai Development Phase II and Central Wanchai Bypass Sampling, Field Measurement and Testing Work (Stage3) Summary for Notification of Exceedance

Ref no.	Date	Tidal	Location	Parameters (Unit)	Measured	Action Level	Limit Level	Follow-up action	
X_19C001	25-Jan-19	Mid-flood	P5	DO(mg/l)	7.57	3.36	2.73	Possible reason:	Natural variation or changes of water quality in the vicinity of water quality monitoring station.
				Turbidity	2.47	9.10	10.25		Immediate repeated in-situ measurement to confirm the exceedances. Checked with Contractor works and reviewed previous monitoring data.
				SS	15.50	15.00	22.13		No marine construction activity was conducted under Contract HK/2012/08 on the monitoring date while the location of the construction area was at downstream of monitoring station P5 during monitoring period. In view of the above, it is considered that the exceedance was not related to Project works.



Appendix 9.1

Complaint Log



## **Environmental Complaints Log**

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Out	come	Status
100321a	21/3/2010	ICC Case no. 1-224618029, Ms. Tsang	Location near Tin Hau	Complaint regarding the loud noise and dark smoke in the course of dredging works on 21 March 2010 (Sunday).		A valid Construction Noise Permit no. GW-RS0119-10 was granted from EPD since 18 <sup>th</sup> Feb. 2010 for the dredging works which carry out at area for North Point Reclamation.	Closed
					2)	Officer from Marine Department, Police and EPD's officer attended the scene for inspection and investigation.	
					3)	The Contractor (CHEC-CRBC JV) strictly comply all the conditions in CNP and take all mitigation measures in order to minimize the potential impacts to surrounding sensitive receivers. A formal letter was issued out by CHEC-CRBC JV and to explain the status of the recent construction activities.	
					4)	No limit level exceedance was recorded on the noise measurement during day time and evening time noise measurement on 23 March 2010. Additional restrict hours noise monitoring at Causeway Bay Community and City Garden was conducted on 5 April 2010 (Public Holiday). No limit level exceedance was recorded in the monitoring.	
					5)	No further complaints were received from Mr. Tsang in the reporting month. The complaint is considered closed.	
100321b	21/3/2010	Unknown	Near the eastern breakwater of the Causeway Bay Typhoon Shelter	from dredging activities on 21/3/2010 (Sunday) until 2220 hours and between 1920-1946 hours in the evening of 22 March	,	A valid Construction Noise Permit no. GW-RS0119-10 was granted from EPD since 18 <sup>th</sup> Feb. 2010 for the dredging works at area for North Point Reclamation during general holidays including Sunday between 0700-2300 hours and any day not being a general holiday between 1900-2300hours. It is complied with the condition of CNP.	Closed
				2010(Monday).	2)	Officer from Marine Department, Police and EPD's officer attended the scene for inspection and investigation.	
					3)	No limit level exceedance was recorded on the noise measurement during day time and evening time noise measurement on 23 March 2010. Additional restrict hours noise monitoring at Causeway Bay Community and City Garden was conducted on 5 April 2010 (Public Holiday). No limit level exceedance was recorded in the monitoring.	
					4)	No further complaints were received in the reporting month. The complaint is considered closed.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Out	tcome	Status	
100504	4/5/2010	Public complainant received by ICC (ICC case: 1- 233384048)	Watson Road	Complaint on the noise nuisance due to the large scale of dredging machine (face to Island East Corridor) in particular the hours 1900 to 0800 and request to reduce the noise level.	,	Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0119-10 for their dredging works. Contractor has implemented mitigation measures to reduce the working hour not later than 2230. According to RSS 's record, no more daytime and night time dredging since the departure of the split hopper barge from the workplace on 29 April 2010 at 1900 hrs to 5 May	Closed	
					3)	2010. No further complaints were received in the reporting month. The complaint is considered closed.		
100731	31/7/2010	Mr. Lee received by ICC (CC Case: 1-250702681)		Complaint on the noise nuisance due to the dredging works. Three construction plants were operated concurrently.	2)	Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0371-10 for their dredging works. There was only 1 grab dredger operated by Contractor within NPR project site area for dredging works.	Closed	
					3)	3)	No noise exceedance was recorded at noise monitoring station at Victoria Centre on 27 July and 3 August 2010 during daytime and evening time period.	
						It is considered as invalid from the EP and CNP point of view.		
100812	12/8/2010	Mr. Wong, Harbour Heights (Management) Ltd.	Harbour Heights	Management office received their resident complained on the noise nuisance from the dredging works at the marine	1)	Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0371-10 for their dredging works. Contractor has implemented mitigation measures to reduce the working hour not later than 2230.	Closed	
		Har	works area adjacent to the Harbour Height during the period from 0700 to 2200.	2)	No noise exceedance was recorded at noise monitoring station at Victoria Centre on 10 and 17 August 2010 during daytime and evening time period.			
					3)	It is considered as invalid complaint. No further complaints were received in the reporting month. The complaint is considered closed.		



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Out	tcome	Status
101108	8/11/2010	Mr. Nip received by ICC (CC Case)	Sai Wan Ho	Visual concern around the seaside silt screen outside the WSD freshwater intake pump at Sai Wan Ho (Monitoring station ref no WSD15)	1) 2) 3)	Contractor for HY/2009/11has been regular checked of condition and removal of trapped rubbish before the dismantling of the floating silt screen to be replaced by wall mount silt screen. Follow-up action had been immediately carried out to check and clear the floating refuse around the seaside silt screen after receipt of the complaint. Removal of seaside silt screen outside the WSD freshwater intake (WSD15) by contractor HY/2009/11 was checked and confirmed dated 9 November 2010. Silt screen has been deployed into the existing steel frame at WSD15 for the protection of WSD salt water intake.	Closed
101110	10/11/2010	Mr. Wong, Harbour Heights (Management) Ltd.	Harbour Heights	Management office received their resident complained on the noise nuisance from the power mechanical equipment during the 0700 to 2200hrs	,	Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0870-10 for their dredging works during evening time. Contractor has implemented mitigation measures to reduce the working hour not later than 2230. No noise exceedance was recorded at noise monitoring station at Victoria Centre on 4 and 10 November 2010 during daytime and evening time period. It is considered as invalid complaint. No further complaints were received in the reporting month. The complaint is considered closed.	Closed
101203	3/12/2010, 01:45a.m.	The resident of Block 11, City Garden by ICC referral from Marine Department	North Point	Bad odour was generated from the dredging plant off North Point		The first investigation was carried out by Marine Department patrol in the morning on 3 Dec 2010 at around 10:00 and revealed that a few working barges were anchoring in the vicinity without carrying out dredging work. A further specific investigation inspection on contractor's backhoe barge in the vicinity of City Garden was jointly conducted with Engineer Representatives (AECOM/RSS), and ET on 8 Dec 2010 at 11:30. No bad odour was noted during the investigation. Routine dredging operation of the backhoe barge was performed during the jointed investigation inspection and it was revealed that no bad odour was attributed by the dredged materials inspected.	Closed
101206	6/12/2010	Ms Lui, the resident of 27/F, Block 10, City	City Garden, North Point	Two barges were generating noise at 22:00 on 6 December 2010 in which the noise from	• • •	ET confirmed the following information with resident site staff on the complaint: • It was referred to the filling operation at North Point	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
		Garden by ICC (ICC case: 1- 266039336)		filling operation was louder than the traffic noise & visual impact was generated due to the spot- light pointing directly to the complainant flat, suspected the filling operation was part of Wanchai Development Phase II; Complainant also raised the same complaint to District Councillor, Mr. Hui on 7 Dec 2010 regarding the night-time noise and suspected earlier start of work at 06:30. Complaint also requested for limiting the plant operating hours from 09:00- 21:00.	<ul> <li>Reclamation of Central Wan Chai Bypass site area instead of part of Wanchai Development Phase II;</li> <li>Two derrick barges were in operation at the time of complaint for placing 400 rockfill onto the excavation trench and for levelling the formation level to receive the pre-cast caisson seawall;</li> <li>Flood light on the control mast of derrick barge have no lighting shields for the prevention of glare of flood lights;</li> <li>No starting work on 7 Dec 2010 at 0630hours.</li> <li>PME used in restricted hours were checked and confirmed compliant with valid CNP no. GW-RS0870-10. The noise level recorded on 6 Dec 2010 was complied with the noise criteria during restricted hour;</li> <li>It was found that the occasional noise nuisance might be caused by the hitting or scratching onto the rock surface during loading down the grab onto the Grade 400 rockfill;</li> <li>The absence of the lighting shields at flood light results in visual glare to the compliant at night-time.</li> <li>Contractor was advised to minimize the finishing time of placing Grade 400 rockfill at 2100hrs and switch off all unnecessary flood lights apart from the light for the safety and security purpose;</li> <li>No further complaint was received after implementation of proposed measures</li> </ul>	
110415	15/04/2011	The resident, Mr Law at Victoria Centre by ICC (ICC#1- 281451236)	North Point	A dust generation and a concern of mosquitoes breeding complaint in which suspected the filling operation was part of North Point Reclamation.	<ol> <li>The concerned stockpile was a working stockpile under Contract HY/209/15 and was covered at night time after work.</li> <li>Water spraying on the haul road and potential dust generating material at least 4 times a day was conducted by contractor that complies with the requirement.</li> <li>It is considered invalid but preventive actions can be taken because the stockpile is relatively large and easily visible by complainant.</li> <li>It was recommended that increasing the frequency of water spraying shall be conducted to all potential dust generating materials and activities. Besides, Contractor should consider to cover the idle part of the stockpile</li> <li>The concern of mosquitoes breeding is out the scope of EM&amp;A, the follow-up action is not reported in this monthly EM&amp;A report.</li> </ol>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Out	come	Status
110419	19/04/2011	Ms Chiu at Victoria Centre at Victoria Centre by	North Point	The episode of night noise on 19/4/11 and 20/4/11 at 2:50 am and the noise lasted for 30 minutes per night.	1)	According to the RSS's record, there was no construction works undertaken under the EP-356/2009 during the concern time period.	Closed
		ICC (ICC# 1- 272874759)		minutes per hight.	2)	There was no abnormal real-time noise monitoring data recorded in RTN1 - FEHD Hong Kong Transport Section Whitefield Depot which is next to the Victoria Centre.	
					3)	It is considered as invalid complaint under this Project.	
110617	9/06/2011	Mr. Law from Victoria Centre Management	North Point	An odour nuisance suspected generating from the discharge point – Channel T at Watson Road in part of the site area was	1)	The complaint was received by ET on 13 Jun 2011. During the weekly site inspection on 7 and 17 June 2011, there was no any odour impact detected in the site area.	Closed
		Office		related to CWB under Contract no. HY/2009/11	2)	According to the site record, there was muddy water discharged from the unknown source at upstream of Channel T during heavy rainstorm. No any site surface runoff to the Channel T and out of site boundary was observed in the inspection.	
			3)	In order to prevent muddy water washing out to the water body under heavy rainstorm, a silt curtain was installed at the outfall of the channel by Contractor. ET confirmed with the Resident Site Staff that a silt curtain was installed at the outfall of the channel to prevent muddy water washing out to the water body under heavy rainstorm. Besides, regular cleaning of refuse in the channel has been conducted by Contractor.			
					4)	A further site investigation on 28 June 2011 revealed that no odour nuisance was detected at the upstream of the Channel T and no source of odour nuisance was identified at site. As such, it was concluded that the source of odour nuisance was not related to the Project works.	
					5)	Although no source of odour nuisance was identified at site, the muddy water and dirt from the unknown source at upstream of Channel T may cause a potential smell during low tide and low water flow. Contractor was reminded to remove the silt curtain at the channel on non-rainy day so as to avoid the accumulation of the sediment and dirt in the water channel.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Out	tcome	Status
110709	09/07/2011	Mr. Au from City Garden Management Office	North Point	A complaint letter to Contractor HY/2009/11 was raised by Cayley Property Management Limit on 9 July 2011 regarding a series of pump breakdown events at seawater intake of City Garden on 4, 6, 7 and 8 July 2011. A lot of rubbish such as plastic bags, nylon bags, nylon- wire mesh was observed sucking from the seawater intake at the seawater front of Block 7 of City Garden affecting the operation of seawater pump plant.	2)	Contractor conducted formation works for installation of caisson seawall at C27, C28, C29 and C30 on 4, 6, 7 and 8 July 2011 and no dredging work was conducted during this time period Water mitigation measures of an 80m long silt curtain at the site boundary in front of City Garden Relocation of silt curtain and silt curtain at the outfall of the channel were provided and maintained to accommodate the site works. All vessels are equipped with rubbish collection facilities and disposed the rubbish regularly. Also, daily cleaning actions had been taken by contractor to minimize floating refuse within the site boundary. Moreover, it has been reported several times that discharged from outfall pipeline outside the site boundary near the intake of the pump maybe considered as another source of rubbish generation.	Closed
					4)	Referring to the record provided by Cayley Property Management Limit, the trapped rubbish was unlikely generated from the construction works. It was considered that complaint is invalid and not related to project.	
110710	09/07/2011	Complainant by ICC (ICC no. 1- 301520309	North Point	It was received at 00:56 on 10 July 2011. There was complained a derrick barge unloading rockfill material off the shore facing the Harbour Grant HK Hotel causing noise nuisance.		ET confirmed with the Resident Site Staff that the complaint was referred to Contract HY/2009/15 for the loading and unloading of fill material at two barges operation in the sea at around 300m adjacent to Island Eastern Corridor (Oil Street Chainage) where is outside the Site of HY/2009/15 in the period of around 19:45 on 9 July to 1:00 on 10 July 2011.	Closed
					2)	The material loading and unloading operation processed in restricted hours was checked without a valid CNP. It was found that the operation was due to an unexpected water leakage of the hopper barge and considered an incident.	
					3)	According to the incident report provided from RSS on 20 July 2011, around 7:30 pm the barge S22 was inclined slightly and slightly water leakage might occur. Due to marine safety concern, the hopper barge would open the hopper to release the contained materials in order to reduce the weight and stabilize the barge. In consider of slight water leakage, the operator decided to use the nearby Derrick Barge ST32 to help for unload the general fill materials first and the unloading operation was started at around 7:45pm, and end at around 1:00 am. Contractor was reminder to provide frequent check of vessel condition	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Out	come	Status
						so as to prevent recurrent by barge defect	
110723a	23/07/2011	Ms. Law at Victoria Centre by ICC no. 1- 303887687		Department published a notice	1) 2)	It was referred by AECOM to ET on 28 July 2011 RSS confirmed that the notice was prepared by Victoria Centre's Management office to their resident and the advice was only given on the extension construction works (for Contract HY/2009/15) to 7am-9pm from Monday to Saturday except Public Holidays and Sundays.	
				Saturday, Sunday and public holiday.	3)	As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am and is expected to be completed by mid- August 2011.	Closed
					4)	No noise exceedance was recorded at construction noise monitoring station at Victoria Centre on 19 and 25 July 2011 during daytime while breaking and excavation works were undertaken during monitoring.	
					5)	In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.	
110723b	23/07/2011	Ms. Yau at Block 2, Victoria Centre by ICC no. 1- 304013959	North Point	Reclamation work was conducted at Causeway Bay Typhoon Shelter at 7am on 23 July 2011. She complained that the works shall be started later to minimize the noise nuisance	1) 2)	It was referred by AECOM to ET on 8 August 2011 With reference to the construction noise monitoring at Vitoria Centre, no exceedance was recorded on 19 and 25 July 2011 during daytime while breaking and excavation works were undertaken during monitoring	
				to the vicinity of the residents in early morning	3)	As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am and is expected to be completed by mid- August 2011.	Closed
					4)	In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.	
110727a	27/07/2011	Mr. Law from Victoria Centre Management Office by ICC no. 1-304616162	North Point	It was complained by Mr. Law from Victoria Centre Management Office on 27 July 2011 regarding construction noise generated by the construction operations of	1) 2) 3)	It was referred by AECOM to ET on 28 July 2011 RSS confirmed to start the rock breaking activities for Contract HY/2009/15 at 8am as a mitigation measure to minimize the noise nuisance in the vicinity of the residents. No noise exceedance was recorded at construction noise	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Out	tcome	Status
				Central-Wanchai Bypass at noon rather than in morning at 7am.		monitoring station at Victoria Centre on 25 July and 4 August 2011 during daytime while breaking and excavation works were undertaken during monitoring.	
					4)	In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. No further complaint from complainant was received after proposed the mitigation measure.	
110727b	27/07/2011	Ms. Chiu by ICC no.1-304615409	North Point	Noise nuisance from the excavation works for the Highways Department adjacent to the Victoria Centre was conducted from 7am	1) 2) 3)	It was referred by AECOM to ET on 28 July 2011 With reference to the construction noise monitoring at Vitoria Centre, no exceedance was recorded on 25 July and 4 and 10 August 2011 during daytime while breaking and excavation works were undertaken during monitoring. As a mitigation measure to minimize the noise nuisance in	
	08/08/2011				4)	the vicinity of the residents, rock breaking activities will be started at 8am. However, complainant did not satisfy with the response on the noise nuisance from the rock-breaking during morning in front of Victoria Centre and then further	Closed
					5)	complaint via 1823 on 7 August 2011. Highways contacted the complainant on 15 August 2011 that the noisy rock breaking operation had been completed.	
					Rer	marks: There will be counted as two complaints in this complaint log.	
110810	10/08/2011	Mr. Yip by ICC no. 1 – 306740207	North Point	Muddy water was discharged from work site to the seafront near Oil Street during heavy rain. The environmental protection measures were not good enough and are needed to rectify.	1) 2)	It was referred by AECOM to ET on 17 August 2011. Confirmed with RE, Muddy water was caused by a heap of earth being washed to the sea by heavy rain. The heap of earth was referred as a small stockpile placed close to the seafront in front of Oil Street within the site area under handover transition period from contract HY/2009/11 to contract HY/2009/19. The necessary mitigation measures to protect the small stockpile against rainfall were missing at the time of complaint.	Closed
					3) 4)	Due to the missing of mitigation measures to protect the small stockpile during handover transition period, loose material was washed into the harbour when heavy rain came. Muddy water was formed and dispersed in the sea that caused the water quality and visual concern to the public. The complaint was considered as valid. Contractors were advised to relocate the loose materials	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Out	tcome	Status
						away from the coastline as far as practicable. Any loose material placed which needed to be placed near the coastline shall be properly compacted or covered as appropriate. To avoid any further environmental deficiency, Contractors shall ensure all necessary environmental mitigation measures will not be missing during site area handover.	
110826	26/08/2011	/2011 Grand Hyatt and a complainant by ICC	wan chai w ar	nuisance generated from the works at Convention Avenue and inside the HKCEC1 reclamation area.	1) 2)	Confirmed with the Resident Site Staff that the construction works were referred to the Contractor HK/2009/01. The Excavator mounted breaker at Convention Avenue and Drilling rig at HKCEC1 reclamation area were the dominant construction noise source during this period.	
					3)	The drilling rig at HKCEC1 reclamation area and excavator mounted breaker at Convention Avenue were then temporary suspended after received the complaint.	
					4)	Investigation revealed that the erected noise barrier (4m cantilevered movable noise barrier for the drilling rig and 1m movable noise barrier for the excavator mounted breaker) were not located close to the plants to provide adequate noise screening.	Closed
					5)	Contractor was advised to avoid concurrent operation of construction plants at site. Further enhancement of movable noise barriers at HKCEC1 and providing noise enclosure for the excavator mounted breaker at Convention Avenue are needed.	
					6)	Further site investigation and checking on 31 August and 7 September 2011 revealed that the implemented noise mitigation measures were in proper and minimize the noise impact.	
110826A	26/08/2011	A complaint letter from Mr. Au of Cayley Property of City Garden	North Point	Harbor front adjacent to their cooling water intake suction which caused 3 times of system breakdown of the sea water pump on 9, 22 and 25 August 2011.	1)	It was referred by AECOM to ET on 29 August 2011. Confirmed with the Resident Site Staff that the • construction works were referred to the Contractors HY/2009/11 and HY/2009/19. • The pump is located on the site area of HY/2009/19 • A temporary garbage defender was installed on 23 July 2011 by HY/2009/11 and the shape of the defender was adjusted on 8 August 2011 in order to excluse the outfall.	Closed
						<ul> <li>An ad hoc inspection of the effectiveness of garbage defender was conducted with RSS (CWB project</li> </ul>	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					team), contractor of HY/200911 and HY/2009/19 and IECon 29 August 2011. Inspection report of it was submitted to RSS on 19 September 2011.	
					<ul> <li>Daily cleaning near the water intake was conducted twice a day by contractor HY/2009/19.</li> </ul>	
					<ul> <li>In response to City Garden request, the contractors have set up the temporary garbage defender in function and collect the floating refuses, but cannot eliminate all refuses, in particular the refuse coming from the seabed</li> </ul>	
					<ol> <li>According to the complaint letter from Cayley Property, the outcomes of the preventive measures were not complying wih their expectation.</li> </ol>	
					3) During on-site inspection, floating refuses observed occasionally outside the garbage defender. No conclusion could be made for the source of these floating refuses. On the other hand, some of the refuses were observed floating behind the garbage defender during investigation.	
					4) All daily cleaning actions had been taken by contractor to minimize floating refuse inside the construction site.	
					5) It was noted that the cooling water intake was accessible to the public. As such, fish breeding and fishing activities were observed even though a notice has already hoisted. Also, tripping of rubbish by the passers-by could result in a lot of rubbish accumulated around the intake point.	
					<ol> <li>Referring to the record provided by CPML, there were a lot of nylon/ plastic bags and nylon wire mesh that matched those rubbishes generated from the public activities.</li> </ol>	
					<ol> <li>Contractors have fulfilled the requirement of site cleanness and no exceedance was recorded during Water Quality Monitoring. It is consider the cause of this complaint is not related to project and environmental issue in this project as well. No more complaint received after ad-hoc inspection</li> </ol>	
111014	14/10/2011	The complainant, Ms. Tam complained via hotline 1823	Wan Chai	The polluted fumes and exhaust from the excavation by sub-contractor of CEDD on pedestrian way outside no.25 Harbour Road (in front of the Harbour Centre)	<ol> <li>RSS notified ET to carry out investigation on 17 October 2011.</li> <li>ET confirmed with the Resident Site Staff that the location of the excavator was within site area of Contract no. HK/2009/02 undertaking the water cooling main reprovision works along the Harbour Road. The plants including the excavator have been checked before using</li> </ol>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<ul> <li>at the site. However, the polluted fumes and exhausted from the excavator was caused due to insufficient maintenance of the plant after using at site.</li> <li>3) After receiving the complaint, the excavator was then</li> </ul>	
					removal off-site for checking and maintenance works on 17 October 2011.	
					<ol> <li>Contractor was reminded to enhance regular checking and maintenance to all plants at site.</li> </ol>	
					<ol> <li>RSS has replied to the complainant on the arrangement of the measures taken on 17 October 2011. Complainant was satisfied with the response and follow-up action taken by the Contractor.</li> </ol>	
111104	04/11/2011	Mr. Liu from LCSD complained via Contractor Complaint Hotline	Wan Chai	Complain about a tree near the site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road, the status is not healthy and roof ball of two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue were half cut.	<ol> <li>ET confirmed with the Resident Site Staff that         <ul> <li>A tree near the site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road is the Tree no. TA1122 under Contract no. HK/2009/02. Leaves of a branch of this tree were shrivelled.</li> <li>Two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue are the tree nos. A160 and A161 under Contract no. HK/2009/01. Part of roof ball of these two trees was covered by the metal plate.</li> </ul> </li> <li>Independent Tree Specialists for these two inspected the trees. Contractor HK/2009/01 has taken the measure as recommend downgrading the soil level around the trunk base. Reinstating of the ground works will be conducted in mid-December 2011. For the tree no. TA1122 under Contract no. HK/2009/02, the brown leaves were removed and fenced the tree with orange net is provided to prevent damage of tree trunk by construction works. The distance between the tree and the edge of the trench is kept approximate 2m. Two Contractors were reminded to carry out regular watering to the trees within their site area.</li> </ol>	Closed
111106	06/11/2011	Police officer	Wan Chai	Construction noise generated from the site at about 6:30 a.m on 6 November 2011 and require to stop the machine operation	<ol> <li>According to the information reported by Contractor, one BC cutter and hoist were operated for Diaphragm Wall construction of Shatin-Central Link to inspect bentonite pipes and ensure no damages and all the joints are tightened in good position. Then, the subcontractor for Diaphragm wall, SAMBO Korean foreman stopped the engine of the BC cutter immediately. The police officer recorded the details and HKID number of the foreman and then left. Due to the different language communication between the police officer and the Korean foreman, no</li> </ol>	Closed



Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Out	come	Status
				2)	CNP was checked by the police officer. ET confirmed with the Resident Site Staff that same issue was also raised out by RSS at about 7:00a.m on the same day. Besides, it was confirmed that there is no valid Construction Noise Permit for the conducted construction works in the period between 2300 and 0700.	
				3)	Due to insufficient communication between Contractor HK/2009/01 and their Korean Sub-contractor, Korean Sub-contractor had not notified to Contractor before carrying out the inspection of the BC cutter, hoists and bentonite pipes at about 6:00a.m to ensure no damages and all the pipe joints should be tightened and in good position.	
				4)	Contractor was advised to enhance the communication between Contractor and sub-contractor and provide sufficient environmental training to all foreman and operators on restricted hour operation. Futhermore, Construction Noise Permit should be checked and in place for the construction works during restricted hour	
				5)	This complaint was considered in relation to the conducted construction works during restricted hours without valid Construction Noise Permit. No more construction works were conducted during night time period. The construction works will be conducted in accordance with the time period stated in valid CNP. This complaint will be kept in view of any follow-up action from the relevant government activities.	
05/04/2012	N/A	North Point	noise from construction sites of CBTS was observed daily before	2)	and the noise level was below 75dB(A). Site inspection for HY/2009/15 was conducted on 10 April 2012. The condition of noise mitigation measures around CBTS was found satisfactory. RSS confirmed that no pilings were performed during the concerned period. The major works included drilling, diaphragm wall construction and excavations. HyD made a reply to the complainant on 16 April 2012 via 1823. HyD replied that the current works at CBTS were	
	Complaint	Complaint and Received By	Complaint       and Received By       Complainant         Image: Complaint in the second	Complaint         and Received By         Complainant           05/04/2012         N/A         North Point         A complaint regarding excessive noise from construction sites of CBTS was observed daily before 7:30am except on public holidays, and the noise source was mainly from piling works. The complainant requested that construction works should start after 8:30am to avoid nuisance to nearby residents and a	Complaint         and Received By         Complainant         2)           05/04/2012         N/A         North Point         A complaint regarding excessive noises of 2)         3)           05/04/2012         N/A         North Point         A complaint regarding excessive noises of 2)         1)           05/04/2012         N/A         North Point         A complaint regarding excessive noises of 2)         1)           05/04/2012         N/A         North Point         A complaint regarding excessive noises of 2)         1)           05/04/2012         N/A         North Point         A complaint regarding excessive noises of 2)         1)           05/04/2012         N/A         North Point         A complaint regarding excessive noises of 2)         1)           05/04/2012         N/A         North Point         A complaint regarding excessive noises of 2)         1)	Complaint         and Received By         Complainant           Complaint         and Received By         Complainant           Complaint         CNP was checked by the police officer.         ET confirmed with the Resident Site Staff that same issue was also raised out by RSS at about 7:00am on the same day. Besides, it was confirmed that there is no valid construction Noise Permit for the conducted construction works in the period between 2300 and 0700.           Use to insufficient communication between Contractor Interform HK2C0091 and their Korean Sub-contractor, Korean Sub-contractor, Africana day out the inspection of the BC cutter, hosts and between Contractor and sub-contractor and provide sufficient environmental training to all foreman and operators on restricted hour operation. Fulthermore, Construction Norks during restricted hour operation. Fulthermore, Construction Norks during restricted hour operation Norks during restricted hours on the construction Norks during restricted hours on the construction Norks during restricted hours on the relevant advised to enhance the communication between contractor and provide sufficient environmental training to all foreman and operators on restricted hour operation. Fulthermore, Construction Norks during restricted hours on the construction Norks during restricted hours on the construction Norks during restricted hours on the relevant government advises.           05/04/2012         N/A         A complaint regarding excessive rise of provide sufficient environ on set form during night time period atteen advised to enhance the construction Norks during restricted hours on the relevant government advises.           05/04/2012         N/A         A complaint regarding excessive rise of the construction Norks during restric



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					from the above works, the Contractor had erected temporary noise barriers and provided noise blankets on plants. RSS would continue to work with the Contractor on the effectiveness of the environmental mitigation measures implemented on site. No further complaint was received after the response.	
130308	06/03/2013	ICC Case#1- 407181502	Tin Hau	A complaint regarding the dropping of fine rock material into surrounding waterbody was observed during rock breaking operation with two excavators in active operation at the Eastern Breakwater of Causeway Bay Typhoon Shelter near the North Point lighthouse.	<ol> <li>RSS notified ET on 8 March 2013</li> <li>ET confirmed with RSS that excavation works, installation of buoy, flashing light and silt curtain and dredging works were undertaken at Eastern Breakwater during the concerned period on 6 March 2013. One backhoe equipped with breaker and one derrick barge were confirmed in operation while another backhoe was at idle during the concerned period on 6 March 2013.</li> <li>Reviewing the photo record provided by RSS, the condition of the silt curtain deployed around the Eastern Breakwater on 6 March 2013 was found to be in good condition. It is considered that the silt curtain was properly in place during the concerned period and the concerned act of dropping of fine rock material was confined within the silt curtain boundary without adverse impact to the nearby water quality.</li> <li>Further follow up was conducted on 12 March 2013 during weekly environmental audit inspection, the silt curtain deployed around the concerned area was found to be maintained in good condition and the water quality at the concerned work area was generally satisfactory. No violation of the Environmental Permit condition was found.</li> <li>The contracotr was advised and committed to implement preventive meaures to miminize the potential impact of work including conducting regular diver check to ensure the integrity and the extend of silt curtain deployment and to provide adequtae back up stock of silt curtain for emergency use.</li> </ol>	Closed
140612	12/06/2014	EPD ref: EP/860/F2/24 Annex IV	Wan Chai	The complaint is regarding to the water quality of the waterfront outside the Hong Kong Academy for Performing Arts Theatre Block, where a large piece of muddy water was found.	letter from EPD (ref: EP/860/F2/24 Annex IV) was received by ET on 13 June 2014.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<ul> <li>the dispersion was observed partly extended beyond outermost layer silt curtain at 1000hrs. Immediate folloup action was requested.</li> <li>3) It is considered that Contractor's mitigation measures would require further review on the effectiveness to avseepage of muddy dispersion such as regular diver inspection check and daily visual checking of silt curtae. Additional silt curtain at marine access zone was instaby Contractor on 12 June 2014 and the double layer scurtain were generally in order. Follow-up inspection v further conducted on 16 June 2014.</li> <li>The Contractor's investigation report on the complaint</li> </ul>	w bid ns. led t as
140723	21/07/2014	ICC Case Ref: 2-341537112	Works area opposite to Ngan Tao Building	The complaint is regarding to construction noise impact to the complainant who could not sleep due to work and machine at the project site opposite to the Ngan Tao Building.	<ul> <li>case was submitted to EPA via email on 18 June 2014</li> <li>Construction noise impact referred by RSS was receibly ET on 25 July 2014</li> <li>ET confirmed with RSS that horizontal cutting and rem of D-wall at Eastern, Southern and Northern side of T: was undertaken by Contractor of HY/2009/15 within Causeway Bay Typhoon Shelter before 23:00hrs on 2 July 2014 that total 3 numbers of derrick lighter and 3 numbers of saw cut machine were in operation, and removal of D-wall at Panel S30A-1 of TS2 was undert by Contractor of HY/2009/15 within Causeway Bay Typhoon Shelter around 00:25hrs to 00:56hrs on 21 J 2014 that total 1 number of derrick lighter was in oper Typhoon Shelter around 00:25hrs to 00:56hrs on 21 J 2014 that total 1 number of derrick lighter was in oper cutting and removal of Diaphragm Wall at Eastern, Southern and Northern side of TS2 was conducted ur HY/2009/15 within Causeway Bay Typhoon Shelter. T 3 nos. of derrick lighter and 3 nos. of saw cut machine were in operation at the above period. From around 00:25hrs to 00:56hrs on 21 July 2014, removal of D-w Panel S30A-1 of TS2 was undertaken by Contractor of HY/2009/15 within Causeway Bay Typhoon Shelter. T 1 no. of derrick lighter was found operating at the abo period</li> <li>It was considered the condition of CNP GW-RS0592-was not fulfilled by the Contractor of HY/2009/15. "Fro 00:25hrs to 00:57hrs on 21 July 2014, the PME(s) (1 Derrick Lighter) on-site could not follow with any giver</li> </ul>	ed Final report (Issue1) issued on 31 July 2014. Further to complainant follow-up, Final report (Issue2) Issued on 12 Aug 2014. al ler stal e 4 n



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<ul> <li>Notwithstanding the above, according to the site recorded provided by the RSS, the derrick lighter was found malfunction at around 23:00hrs on 20 July 2014 while the diaphragm wall cutting procedure was incomplete. Under safety and navigation consideration, the completion of diaphragm wall removal was necessary and of imminent need.</li> <li>5) The Contractor of HY/2009/15 was advised to review the construction sequence and emergency response procedure for construction activities during restricted hours and night time period to allow for sufficient buffer time for work completion such that the Construction Noise Permit would be followed. Furthermore, the Contractor of HY/2009/15 was suggested to conduct throughout checking of PME used on site prior to work commencement to minimize the potential malfunctioning of PME during the course of work which affect the duration of works.</li> </ul>	
141016	14/10/2014	EPD Ref.: EP860/E2/24 Annex IV ICC complaint received by ET on 10 October 2014	Work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	Construction noise like piling works was heard on 14 October 2014 night until 23:45 hrs. It was suspected that the noise was emanated from the work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	A public complaint regarding construction noise impact referred by EPD was received by ET on 16 October 2014 (EPD Ref.: EP860/E2/24 Annex IV dated 16 October 2014). The complainant reported that construction noise like piling works was heard on 14 October 2014 night until 23:45 hrs. It was suspected that the noise was emanated from the work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	Interim investigation report submitted to EPD on 23 October 2014.
					<ul> <li>ET confirmed with the Resident Site Staff that From 19:00hrs to 23:00hrs on 14 October 2014, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area.</li> <li>Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.</li> <li>From 23:00 hrs to 05:00 hrs, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area.</li> <li>Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.</li> </ul>	Updated interim investigatio n with supplement ary information submitted to EPD on 17 November 2014 EPD



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					From 23:00 hrs to 06:00hrs, panel replacement works was conducted under Contractor of HK/2009/02 at the Temporary Covered Walkway.	advised no further comment
					Total one scissor platform and two hand held drills (battery) were in operation.	on the updated interim
					From 23:00 hrs to 06:00hrs, trial pit works was conducted under Contractor of HK/2009/02 at Hung Hing Road.Total one crane lorry was in operation.	report and case closed on 27 Nov 2014.
					According to the relevant site records under Contract HK/2009/02, from 19:00hrs to 23:00hrs on 14 October 2014, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.	
					From 23:00 hrs to 05:00 hrs, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area.Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.	
					From 23:00 hrs to 06:00hrs, panel replacement works was conducted under Contractor of HK/2009/02 at the Temporary Covered Walkway. Total one scissor platform and two hand held drills (battery) were in operation.	
					From 23:00 hrs to 06:00hrs, trial pit works was conducted under Contractor of HK/2009/02 at Hung Hing Road. Total one crane lorry was in operation.	
					In view of the above findings, no direct information associated with the noise concern was considered available.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
141110	07/11/2014	EPD Ref.: H05/RS/000278 15-14	Construction site at old Wan Chai Ferry Pier	Malodour of construction plant exhaust from the construction site at old Wan Chai Ferry Pier	A public complaint regarding odour concern referred by EPD was received by ET on 07 November 2014 (EPD Ref.: H05/RS/00027815-14 dated 10 November 2014).	Interim investigation report
		EPD complaint received by ET on 10 November		was scented that affecting the swimmers at Wan Chai Swimming Pool.	The complainant reported that Malodour of construction plant exhaust from the construction site at old Wan Chai Ferry Pier was scented that affecting the swimmers at Wan Chai Swimming Pool.	submitted to EPD on 17 November 2014.
	2014				ET confirmed with the Resident Site Staff that	1
			ELS works was conducted on 7 November 2014 during daytime at Portion 2 (Area oppsite to WanChai Swimming Pool).	EPD advised no comment on the interim		
		Total 3 nos. of excavators, 2 nos. of crawler cranes, 2 nos. of generator, 1 no. of crane lorry and 2 no. of dump trucks were operated.	report and case closed on 1 Dec 2014.			
		Demolition works was conducted on 7 November 2014 during daytime at West of old Wan Chai Ferry Pier.	2011.			
			Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. of tug boat were operated.			
					Dredging works was conducted on 7 November 2014 during daytime at WCR3 (East of old Wan Chai Ferry Pier)	
					Total 1 no .of dredger, 1 no. of hopper and 1 no. of tug boat were operated.	
					According to the relevant site records under Contract HK/2009/02, ELS works was conducted on 7 November 2014 during daytime at Portion 2 (Area oppsite to WanChai Swimming Pool). Total 3 nos. of excavators, 2 nos. of crawler cranes, 2 nos. of generator, 1 no. of crane lorry and 2 no. of dump trucks were operated. Demolition works was conducted on 7 November 2014 during daytime at West of old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. of tug boat were operated.	
					Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on- site. The condition of chemical waste storage was considered satisfactory and no malodour was identified. Despite no information related to malodour was identified, the Contractor was reminded to conduct regular checking on the condition of PMEs to ensure only well maintained PMEs are used on site.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Based on the relevant information provided by RSS, despite no information associated with the malodour concern was identified after investigation, the Contractor was reminded to conduct regular checking on the condition of PME used on site to ensure only well maintained PME are used on site The interim report would be submitted to EPD on 17 November 2014.	
141113	12/11/2014	EPD Ref.: H05/RS/000282 53-14 EPD complaint received by ET on 13 November 2014	Construction site at old Wan Chai Ferry Pier	Malodour and dark smoke emission from an excavator located at the construction site at old Wan Chai Ferry Pier was observed that affecting the pedestrians.	A public complaint regarding odour concern referred by EPD was received by ET on 13 November 2014 (EPD Ref.: H05/RS/00028253-14 dated 13 November 2014). The complainant reported thatMalodour and dark smoke emission from an excavator located at the construction site at old Wan Chai Ferry Pier was observed that affecting the pedestrians. (Contract HK/2009/02) ET confirmed with the Resident Site Staff that demolition works was conducted under Contract HK/2009/02 on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated. According to the relevant site records under Contract HK/2009/02, demolition works was conducted on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated. In addition, investigation found that due to malfunctioning of one of the excavators deployed at old Wan Chai Ferry Pier, dark smoke was emitted from the defective excavator for a short period of approximately 30 seconds at around 15:00 hrs on 12 November 2014. The operation of excavator was immediately suspended and followed by repair works. The normal operation of the excavator was resumed after repair. Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on- site and the Contractor of HK/2009/02 was reminded to conduct regular checking on the condition of PMEs to ensure only well maintained PMEs are used on site.	Interim investigation report submitted to EPD on 19 November 2014. EPD advised no comment on the interim report and case closed on 8 Dec 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
141121	Not Specified	EPD Ref: H08/RS/28263-14 EPD complaint information and findings was received by ET via email on 21 Nov 2014	Causeway Bay Typhoon Shelter	Resident in Hing Fat Street complaining about loud noise from dredging work in CBTS up to 10pm at night.	<ul> <li>EPD received a construction noise complaint from dredging works at Causeway Bay Typhoon Shelter and a resident in Hing Fat Street complaining about loud noise from dredging work in CBTS up to 10pm at night.</li> <li>EPD investigation found that the operation of a derrick barge is covered by CNP no. GW-RS0701-14.</li> <li>EPD reminded the Contractor of HY/2011/08 to ensure the work strictly follow the permit conditions and endeavor to minimize the noise as so not to disturb the nearby residents.</li> </ul>	Complaint case handled by EPD and relevant investigation findings was sent to ET on 21 November 2014
150127	21 Jan 2015	EPD complaint (EPD Ref.: H05/RS/00001 725-15) received by ET on 27 January 2015 and further information from EPD regarding the updated location under complaint was received by ET on 30 January 2015	A portion of Hung Hing Road immediately to the east of Marsh Road near SPCA	Construction dust and grit was emitted from the construction site to the carriageway causing nuisance to the public.	A public complaint regarding air quality impact referred by EPD was received by ET on 27 January 2015 (EPD Case Ref.: H05/RS/00001725-15 dated 27 January 2015) and further information from EPD regarding the updated location under complaint was received by ET on 30 January 2015. The complainant reported that construction dust and grit was emitted from the construction site to the carriageway causing nuisance to the public. ET confirmed with the Resident Site Staff that the major construction activities around the concerned location conducted on 21 January 2015 include breaking of seawall blocks and D-wall at TPCWAW; concreting, grouting and drilling works at TPCWAW;reclamation/ backfilling works at TPCWAW Mitigation measures implemented by the Contractor for the above construction works include spraying haul road with water; covering bagged cement with tarpaulin; providing three sided and top covering for grouting stations; providing water spraying to dusty activities such as breaking works According to the relevant site records, breaking of seawall blocks and D-wall, concreting, grouting and drilling works and reclamation/ backfilling works were	Interim report submitted to EPD on 9 February 2015, EPD advised no comment on 27 February 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					conducted at TPCWAW. Dust mitigation measures including spraying haul road with water, covering bagged cement with tarpaulin, providing three sided and top covering for grouting stations and water spraying to dusty activities such as breaking works were implemented by the Contractor of HY/2009/15 near the concerned location on 21 January 2015.	
					Follow-up investigation was conducted on 27 January 2015 during weekly environmental inspection, dust mitigation measures including water spraying for dusty haul road and major dust generation works; and provision of three sides and top covering for grouting station were confirmed in place.	
					In addition, based on the review of the monitoring data of the monitoring station located at the concerned location raised by the complainant, namely monitoring station CMA3a, no action or limit level exceedance was recorded during air quality monitoring conducted on 20 and 21 January 2015. Nevertheless, the Air Quality Health Index (AQHI) recorded by EPD across Western District and Eastern District on the complaint date was ranged from 4 to 10+ indicating a severely high concentration of ambient air pollutants.	
					As such, the site condition under Contract HY/2009/15 at the concerned location was considered to be generally satisfactory and no non-conformity related to cumulative air quality impact was observed. Nevertheless, in view of the public concern, the contractor was reminded to enhance the dust mitigation measures implemented to minimize potential nuisance to nearby public.	
150622	18 June 2015	EPD Ref.:H05/RS/ 00015054-15 dated 8 June	A mooring location near shore and at location outside Wan Chai Sports	Dark smoke and malodour emission was observed from a hopper barge moored near shore and	A public complaint regarding dark smoke and malodour concern referred by EPD was received by ET on 22 June 2015 (EPD Ref.: H05/RS/00015054-15 dated 22 June 2015). The complainant reported that dark smoke and malodour emission was observed from a hopper barge	Interim report submitted to EPD on 29 June 2015 and EPD



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				Nature of Complaint other construction plants under operation from the reclamation construction site	<ul> <li>moored near shore and other construction plants under operation from the reclamation construction site with Contract no. HK/2009/02 at location outside Wan Chai Sports Ground caused air pollution. The complainant alleged that the said situation had been observed for a prolonged period.</li> <li>ET confirmed with the Resident Site Staff that reinforced bar fixing and concreting work (on 17 June 2015 only) were conducted at Portion 2 from 15 June 2015 to 19 June 2015. Total 3 nos. of mobile crane were in operation. Dn 17 June 2015, one no. of concrete pump truck and two nos. of concrete mixer were in operation. Excavation and Lateral Support was conducted at Portions 3 &amp; 4 from 15 June 2015 to 19 June 2015. Total 4 nos. of excavator, 2 nos. of truck and 2 nos. of crawler crane were in operation. In addition, on 15 June 2015, 17 June 2015 and 19 June 2015, 1 no. of derrick barge was moored near Portions 3 &amp; 4 for transportation of the excavated material away from site.</li> <li>According to the relevant site records under Contract HK/2009/02, from 15 June 2015 to 19 June 2015, reinforced bar fixing and concreting work (on 17 June 2015 only) were conducted at Portion 2 and total 3 nos. of mobile crane, one no. of concrete pump truck (on 17 June 2015 only) and two nos. of concrete mixer (on 17 June 2015 only) were in operation; excavation and</li> </ul>	Status advised no comment on 20 July 2016 on the interim report submitted and case closed.
					lateral support was conducted at Portions 3 & 4 and total 4 nos. of excavator, 2 nos. of truck and 2 nos. of crawler crane were in operation. Based on relevant site record, no hopper barge was moored under Contract HK/2009/02 around the concerned location while 1 no. of derrick barge was moored under Contract HK/2009/02 near Portions 3 & 4 for transportation of the excavated material from Portions 3 & 4 away from site on 15 June 2015,17 June 2015 and 19 June 2015 respectively.	
					Follow-up inspection was conducted during weekly	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
Log No.	20 July 2015	EPD Ref.:H05/RS/ 00018040-15 dated 23 July 2015	Complainant Ex-Wanchai Ferry Pier near 720 & & 722 Bus stop	Malodour from marine sediment	<ul> <li>environmental inspection on 25 June 2015, no dark smoke and malodour emission was observed from the PMEs operating on-site. A derrick barge was observed moored near Portions 3 &amp; 4 and excavated material was transferred to the derrick barge by the excavators on land without barge operation and no particular dark smoke and malodour emission was observed. Nevertheless, the Contractor was reminded to conduct regular checking on the condition of the derrick barge and other PMEs deployed on site to ensure only well maintained PMEs are used to avoid potential dark smoke and maldour emission affecting nearby public.</li> <li>A public complaint regarding malodour referred by EPD was received by ET on 23 July 2015 (EPD Ref.: H05/RS/00018040-15 dated 23 July 2015).</li> <li>The complainant reported that malodour from marine sediment was scented at ex-Wanchai ferry pier near route 720 &amp; 722 bus stop. (Contract HK/2009/02).</li> <li>ET confirmed with the Resident Site Staff that Rockfill placing works was conducted by one derrick barge at the concerned location (WCR3) under Contract HK/2009/02 on 20 July 2015. No marine sediment was stored or placed on site at the concerned location under Contract HK/2009/02, rockfill placing works was conducted by one derrick barge at the concerned location on the concerned location on the concerned date. Follow-up inspection was conducted during weekly environmental inspection on 29 July 2015. No marine sediment was doserved stored or placed at the concerned location was conducted during weekly environmental inspection on 29 July 2015. No marine sediment was doserved at excord at the concerned location while it was noted that a culvert outfall with potential odour concern is located adjacent to</li> </ul>	Interim report submitted to EPD on 30 July 2015. EPD advised no comment on 17 August 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Nevertheless, the Contractor was reminded to review the handling procedures in case of any future marine sediment handling at the concerned location and to consider the implementation of mitigation measures as appropriate to minimize potential malodour impact to nearby public.	
150904	01 Sept 2015	EPD Ref.: H05/RS/0002 2241-15 dated 04 September 2015 received by ET on 4 September 2015	East of New WanChai Ferry Pier	Dropping of excavated material from land to sea during laoding of material	A public complaint regarding dropping of excavated material from land to sea referred by EPD was received by ET on 04 September 2015 (EPD Ref.: H05/RS/00022241-15 dated 04 September 2015). The complainant reported that dropping of excavated materials from land to sea during loading of materials by excavator at the construction site to work boat. (Contract HK/2009/02) ET confirmed with the Resident Site Staff that transferring of C&D materials from land to hopper barge by excavator at seaside along CWB Tunnel Portions 3 and 4 was undertaken by Contract HK/2009/02 on 01 September 2015. Mitigation measure including providing tarpaulin sheet to cover the gap between seawall and the hopper barge to prevent dropping of material to the sea was implemented by the Contractor. According to the relevant site records under Contract HK/2009/02, transferring of C&D materials from land to hopper barge by excavator at seaside along CWB Tunnel Portions 3 and 4 was carried out on 01 September 2015 and mitigation measures including provision of tarpaulin sheet between seawall and the hopper barge was implemented by the Contractor of HK/2009/02 on the concerned date. Follow-up inspection on 10 September 2015. Transferring of C&D materials from land to barge by excavator was observed at the concerned location and mitigation measures including provision of tarpaulin sheet between seawall and the hopper barge was implemented by the Contractor of HK/2009/02 on the concerned date. Follow-up inspection	Interim report submitted to EPD on 14 September 2015. EPD advised no comment on 5 October 2015 on the interim report submitted and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					barge and the material transfer works was generally in order. Nevertheless, the Contractor of HK/2009/02 was reminded to maintain the handling procedure for C&D materials transfer from land to hopper barge and regularly inspect the condition of the tarpaulin sheet provided to ensure the nearby water quality are not affected by the loading and unloading of material from land side to hopper barge. The Contractor was reminded to maintain the handling procedure for C&D materials transfer from land to hopper barge and regularly inspect the condition of the tarpaulin sheet provided to ensure the nearby water quality are not affected by the loading and unloading of material from land side to hopper barge.	
150904	02 Sept 2015	EPD Ref.: H04/RS/0002 2385-15 dated 04 September 2015 received by ET on 04 September 2015	Location outside Fleet Arcade	Construction noise was generated from the construction site of HK/2012/08 at location outside Fleet Arcade during night time on weekdays and daytime during General Holidays. The complainant also concerned construction dust and exhaust emission from derrick barges during transporting C&D material at the site.	A public complaint regarding construction noise and dust and exhaust emission referred by EPD was received by ET on 04 September 2015 (EPD Ref.: H04/RS/00022385-15 dated 04 September 2015). The complainant reported that construction noise was generated from the construction site of HK/2012/08 at location outside Fleet Arcade during night time on weekdays and daytime during General Holidays. The complainant also concerned construction dust and exhaust emission from derrick barges during transporting C&D material at the site. (Contract HK/2012/08) ET confirmed with the Resident Site Staff that from 0800 hrs to 1800 hrs on 30 August 2015, removal of scaffold and timber and installation of bulkhead was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one generator and one circular saw were in operation. From 1900hrs on 30 August 2015 to 0700 on 31 August 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location.	Interim report submitted to EPD on 14 September 2015. 2 <sup>nd</sup> interim report submitted to EPD on 17 Dec 2015 3 <sup>rd</sup> interim report submitted to EPD on 31 Dec 2015



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					From 1900hrs on 31 August 2015 to 0700hrs on 01 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. From 1900hrs to 2115 hrs on 01 September 2015, unloading of soil was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one derrick barge was in operation. From 2300hrs on 01 September 2015 to 0700hrs on 02 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. One derrick barge was deployed for unloading of soil on 02 September 2015 during daytime under Contract HK/2012/08 at the concerned location. Based on the relevant site records, from 0800 hrs to	
					1800 hrs on 30 August 2015, removal of scaffold and timber and installation of bulkhead was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one generator and one circular saw were in operation and the relevant Construction Noise Permit GW-RS0296-15 for the concerned operation was confirmed in place.	
					From 1900hrs on 30 August 2015 to 0700 on 31 August 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location and from 1900hrs on 31 August 2015 to 0700hrs on 01 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location.	
					From 1900hrs to 2115 hrs on 01 September 2015, unloading of soil was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one derrick barge was in operation and the Construction Noise Permit GW-RS0296-15 for the concerned operation was confirmed in place.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					From 2300hrs on 01 September 2015 to 0700hrs on 02 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. In view of the above, the construction activities conducted under Contract HK/2012/08 during the concerned period was in compliance with the statutory requirement.	
					In addition, one derrick barge was deployed for unloading of soil on 02 September 2015 during daytime under Contract HK/2012/08 at the concerned location. Follow-up inspection was conducted during weekly environmental inspection on 08 September 2015 and no dark smoke emission was observed from the derrick barge moored outside the concerned location. Nevertheless, the Contractor of HK/2012/08 was reminded to conduct regular checking on the condition of the all derrick barges deployed on site to ensure only well maintained equipment are used to avoid potential dark smoke emission affecting nearby public and the Contractor of HK/2012/08 was reminded to upkeep the site control system for construction works carrying out at restricted hours and night time for Construction Noise Permit compliance.	
					The Contractor was reminded to conduct regular checking on the condition of derrick barges deployed on site to ensure only well maintained equipments are used on site to avoid potential dark smoke emission affecting nearby public.	
					The Contractor of HK/2012/08 was reminded to upkeep the site control system for construction works carrying out at restricted hours and night time for Construction Noise Permit compliance.	
150917	17 Sep 2015	A public complaint regarding water quality referred by EPD was	Central and Wan Chai Reclamation coastline (between LUNG WUI ROAD to LUNG WO ROAD,	Silt from Central and Wan Chai Reclamation was spotted along the coastline (between LUNG WUI ROAD to LUNG WO ROAD, Central & Wan	Based on the site records confirmed by RSS, removal of seawall blocks by derrick barge was undertaken by Contract HK/2012/08 at Central Reclamation Phase III works area while mitigation measures including provision of silt curtain implemented by the Contractor of HK/2012/08 during the	Interim investigation report submitted to EPD on 25



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
		received by ET on 17 September 2015	Central & Wan Chai, Hong Kong)	Chai, Hong Kong)	seawall block removal works. According to relevant record, muddy dispersion at HKCEC2W (area opposite to Lung King Street) was observed by the Environmental Team on 14 September 2015 afternoon. The muddy patch was observed dispersing outside the outer layer silt curtain deployed by the Contractor of HK/2012/08 towards the Central Reclamation Phase III area while the outer layer silt curtain was observed partially opened.	September 2015. EPD advised no comment on 14 October 2015 and case closed.
					In view of the above observations, the Contractor was advised to rectify any environmental deficiencies such that adequate protection such as silt curtain shall be provided for exposed soil slope to mitigate for potential runoff related water quality impact to the surrounding waters; outer layer silt curtain deployed shall be entirely closed during works to safeguard the surrounding water quality. Any opening for marine vessel shall be closed promptly after passage and localized silt curtain deployed on site shall be properly maintained to avoid any gap or opening to effectively safeguard the nearby waters.	
151015	11 Oct 2015	A public complaint regarding direct discharge of muddy effluent referred by RSS was received by ET on 14 October 2015	Seafront opposite to Watson Road adjacent to Eastern Breakwater	Pink fluid was observed discharged into marine waters at seafront opposite to Watson Road adjacent to the Eastern Breakwater on 11 October 2015.	Based on the site records confirmed by RSS, no construction activity near the seaside between Eastern Breakwater and the Dumping Jetty was undertaken by Contract HY/2009/19 while at site area away from the seawall, construction of EVB substructure, EVB and APS structure was undertaken on 11 October 2015. In addition, no works involving the use of paint was carried out at the concerned site area (Site Portion between Eastern Breakwater and the Dumping Jetty) and along the alignment of the Culvert T1 under Contract HY/2009/19 and no temporary storage of paint was located at the concerned site area and along the alignment of the Culvert T1 under HY/2009/19 on 11 October 2015.	HyD will consolidate all input from relevant parties to form a reply to ICC.
					Follow-up inspection was conducted during weekly environmental inspection on 14 October 2015. No construction works involving the use of paint was observed undertaken at the concerned location while a few number of small containers of paint was observed placed around the concerned location and the paint containers were sealed and no sign of leakage was observed. The few containers were further checked and was found not matching the pink fluid observed on the complaint date. On the other hand, a culvert discharge outfall was found located within the concerned area where the pink fluid was observed. Based on the above, no direct information indicating the pink	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					fluid was originated from the worksarea under HY/2009/19 was considered available. Nevertheless, the Contractor was reminded that paints stored on site shall be properly labelled and stored in sealed container at weather proof location to avoid potential spillage.	
151028	26 Oct 2015	A public complaint regarding construction noise impact referred by EPD was received by ET on 28 October 2015 (EPD Ref:H05/RS/00 027330-15 Dated 28 October 2015)	Construction Site next to ex-Wan Chai Ferry Pier	Operation of grab dredger at construction site near the ex- Wan Chai Ferry Pier from around 0100 to 0400 hours on 26 October 2015 caused noise nuisance.	According to the relevant site records under Contract HK/2009/02, from 01:00hrs to 04:00hrs on 26 October 2015, rock filling was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02 and the relevant Construction Noise Permit GW-RS1121-15 for the concerned construction works was in place. The construction activity conducted under Contract HK/2009/02 during the concerned period was in compliance with the statutory requirement. Nevertheless, the Contractor was reminded to upkeep the site control system for construction works carrying out at restricted hours and night time for Construction Noise Permit compliance in view of the nearby public concern.	The interim report would be submitted to EPD on 05 November 2015 and EPD advised no comment on 16 November 2016 and case closed.
151116	13 November 2015	A public complaint regarding water quality referred by EPD was received by ET on 16 November 2015 (EPD Ref: H05/RS/000291 26-15)	Construction Site at HKCEC and seafront outside Lung Wo Road	Muddy water was discharged from the construction site at HKCEC and dispersed to seafront outside Lung Wo Road on 13 November 2015 afternoon. The complainant also alleged that the deployment of the silt curtain did not follow the design requirement under the environmental permit that the curtain should be hanged to seabed level	Based on the site records, rock mound trimming works was conducted under Contract HK/2012/08 at HKECE2 area on 13 November 2015 and mitigation measures including provision of localized silt curtain around the works area was implemented by the Contractor. Follow-up inspection was conducted during weekly environmental inspection on 17 November 2015, both outer layer silt curtain and localized layer of silt curtain around the active works area were observed deployed while the localized silt curtain deployed around the marine works area was observed partially opened for marine access. Despite no muddy dispersion was generated around the localized silt curtain enclosed area, the Contractor was advised to promptly improve the condition of the silt curtain to ensure the effectiveness of the mitigation measure deployed and to ensure the silt curtain is closed after marine vessel movement. Based on further review on the current construction stage at HKECE2, the dredging works and trench filling works were completed and filling works were conducted behind seawall or temporarily seawall in form of rockbund, the outer layer of silt curtain currently serves as the additional mitigation measure to	The interim investigation report would be submitted to EPD on 1 December 2015 and record of diving inspection conducted on 27 November 2016 was forwarded to EPD on 4 Dec 2016. EPD advised no further comment on 14 Dec 2015 and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					the required silt curtain deployment for safeguarding the water quality in the area. To clarify for the current silt curtain arrangement, the Contractor was advised to submit an updated silt curtain deployment plan with respect to the latest silt curtain arrangement for the current construction stage. In addition, contaminated discharge at Culvert L originating from upstream locations was intermittently observed based on previous site records. Nevertheless, in view of the public concern, the Contractor was reminded to conduct regular checking on the condition and maintenance for the silt curtain deployed on site to ensure the effectiveness of the mitigation measure. A joint meeting for the complaint was held amongst the EPD, WDII RSS team, the ET and the Contractor of HK/2012/08 on 24 November 2015 and a joint silt curtain diver inspection check amongst EPD, ET, IEC, WDII RSS and the Contractor was conducted on 27 November 2015 to confirm the silt curtain condition and the silt curtain deployed at the HKCEC2 water channel was found generally in order.	
160413 (HK20120 8)	13 April 2016	A public complaint referred by EPD was received by ET on 13 April 2016 (EPD Ref.: H05/RS/00008 367-16 dated 13 April 2016)	Outside the Hong Kong Academy for Performing Arts	Muddy water discharge from construction site	A public complaint regarding muddy water discharge referred by EPD was received by ET on 13 April 2016 (EPD Ref.: H05/RS/00008367-16 dated 13 April 2016). The complainant reported that muddy water was discharged from the construction work of Contract HK/2012/08 to the sea outside the Hong Kong Academy for Performing Arts on 13 April 2016 morning. ET confirmed with the Resident Site Staff that internal transport of soil to the hopper barge for storage via landing barge was conducted by Contractor of HK/2012/08 during 0800 hours to 1000 hours on 13 April 2016 at the sea outside the concerned location and 3 nos. of dump trucks were deployed for the operation. Protection measure including provision of sandbag bunding along the side of the landing barge was implemented by the Contractor of HK/2012/08.	Interim investigation report was submitted to the EPD on 21 April 2016. EPD advised no further comment on 6 June 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					April 2016 at the sea outside the concerned location and 3 nos. of dump trucks were deployed for the operation. Protection measure including provision of sandbag bunding along the side of the landing barge was implemented by the Contractor of HK/2012/08. In addition, amber rainstorm warning signal was hoisted from 0630 hours to 1200 hours on 13 April 2016 and during the above time period, muddy water was observed from the upstream of culvert L outside the HK/2012/08 site.	
					Follow up inspection was conducted on 19 April 2016, protection measures including provision of sandbag bunding along the side of the landing barge was implemented and no mud or soil deposition was observed along the seawall and no discharge point was located within the temporary water channel connecting the Culvert L outfall location to the Victoria Harbour. In addition, piling works was observed at the north side of Zone A1 on 19 April 2016 and construction effluent collection from piling work via sedimentation tank to wastewater treatment facility was implemented and steel barrier was installed around the piling works area to mitigate against potential surface runoff related impact.	
					Nevertheless, in view of the public concern, the Contractor was reminded to maintain adequate perimeter embankment protection along the seawall boundary and maintain proper construction effluent collection system to avoid potential runoff related impact to nearby waters.	
160706	30 June 2016	A public complaint referred by EPD was received by ET on 06 July	Construction area near Royal Hong Kong Yacht Club	Derrick barge moored near Royal Hong Kong Yacht Club emitted dark smoke since mid of June 2016.	A public complaint referred by EPD was received by ET on 06 July 2016 (Case Ref.: H05/RS/0016226-16). The complainant reported that a derrick barge in green colour under Contract HY/2009/15 moored near Royal Hong Kong Yacht Club emitted dark smoke since mid of June 2016.	Interim report was submitted to EPD on 14 July 2016.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
		2016 (Case Ref:. H05/RS/00016 226-16),			ET confirmed with Resident Site Staff that the concerned green derrick barge was identified as Yue Fat 206 (YF 206) and the concerned green derrick barge was operated within the Ex-PCWA area for excavation works intermittently across the period from 15 June 2016 to 30 June 2016. The concerned green derrick barge YF206 within Ex-PCWA area was no longer deployed under Contract HY/2009/15 after 02 July 2016. Follow-up inspection was conducted on 11 July 2016, the concerned derrick barge YF206 was not deployed at the concerned location and no dark smoke was observed from other derrick barge operating on-site. Nevertheless, in view of the public concern, the Contractor of HY/2009/15 was reminded to conduct regular checking and maintenance of all derrick barges deployed on site to ensure only well maintained equipment is used to avoid potential dark smoke	EPD advised no further comment on 20 September 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
160825	25 August 2016	A public complaint referred by EPD was received by ET on 25 August 2016 (Case Ref.: H08/RS/00012 592-16)	East of Temporary Reclamation Zone TS3, Causeway Bay Typhoon Shelter	Muddy water was observed at Causeway Bay Typhoon Shelter	A public complaint referred by EPD was received on 25 August 2016 (Case Ref.: H08/RS/00012592-16). The complainant reported that muddy water was observed at Causeway Bay Typhoon Shelter. ET confirmed with the Resident Site Staff that no marine construction activities were undertaken at the concerned location at East of Temporary Reclamation Zone TS3 within Causeway Bay Typhoon Shelther from 14:00hrs to 17:00hrs on 25 May 2016. Site control measures including the following were implemented by the Contractor of HY/2010/08 around the concerned location. Site control measures including i) Wastewater treatment facilities (AquaSed) were installed at TS3 for treatment of wastewater generated during construction activities. Sampling of effluent from AquaSed was conducted by the Contractor of HY/2010/08 and all results complied with the requirements in the Discharge Licence. Visual inspection and pH measurement of effluent were conducted daily by Environmental Supervisors and all results passed. ii) Brick/ earth/ sandbag bunds were installed alongside the site perimeter of TS3 to prevent muddy runoff into the sea. iii) Piping with idled ends were removed to prevent accidental discharge of untreated wastewater. iv) Diver inspection for silt curtains and/ or impermeable barriers was conducted on an ad-hoc basis. vii) Temporary cut slopes were shotcreted or properly covered with tarpaulin sheets. viii) Regular inspections were conducted by the RSS and Contractor's environmental representatives on regular basis on the conditions of mitigation measures implemented on site. Based on the complainant photo information, the exposed soil slope at Temporary Reclamation Zone TS3 were observed protected by covering and enclosed by double layer of impermeable barrier/ silt curtain and no contaminated discharge was identified. In addition, based on information from Hong Kong Observatory, the tidal condition on 25 May 2016 afternoon was found to	The Interim investigation report was submitted to EPD on 2 September 2016. EPD advised no further comment on 31 October 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					be ebb-tide while non construction works marine vessel movements around the identified muddy plume within Causeway Bay Typhoon Shelter was observed in the complainant photo information.	
					Based on review on relevant records, no contaminated surface runoff and no contaminated discharge was identified at the concerned location during the environmental site inspection conducted on 25 May 2016. Follow up inspection was conducted on 31 August 2016 and seawall construction and filing works at the Temporary Reclamation Zone TS3 was observed completed. No contaminated discharge and no contaminated surface runoff was found.	
					Nevertheless, the contractor of HY/2010/08 was reminded to maintain appropriate bunding at seawall boundary for protection against potential surface runoff related impact. Also, the Contractor of HY/2010/08 was reminded to maintain proper site drainage for effluent collection and treatment system to ensure the compliance with relevant discharge license.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
180625	5 June 2018	An EPD complaint was referred to the ET on 25 June 2018 (CASE Ref: H05/RS/00001 5459-18)	Site outside Lung Wo Road	Muddy water discharge was found at the site outside Lung Wo Road on 5 June 2018 afternoon.	An EPD complaint was referred to the ET on 25 June 2018 (CASE Ref: H05/RS/000015459-18). The complainant reported that muddy water discharge was found at the site outside Lung Wo Road on 5 June 2018 afternoon. ET confirmed with the Resident Site Staff that installation of metal formwork at seawall was carried out on 5 June 2018 afternoon and mitigation measure including placing rock fill material on slope surface was implemented at the concerned location to reduce surface runoff. Follow up site inspection was conducted by the Environmental Team on 26 June 2018, no muddy water discharge or surface runoff related water quality impact was observed at construction area under HK/2012/08 near the concerned area Nevertheless, in view of the public concern, the Contractor of HK/2012/08 was reminded to provide addition tarpaulin covering to the slope surface along the seawall around the concerned location to reduce the potential surface runoff and maintain regular checking on the embankment condition to ensure no gap / void to avoid potential seepage / surface runoff to nearby water	The interim report will be submitted to EPD on 4 July 2018. EPD advised no comment on 28 September 2018 on the interim investigation report and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
180625	11 June 2018	An EPD complaint was referred to the ET on 25 June 2018 (CASE Ref: H05/RS/00015 954-18).	Construction Site near Wan Chai Pier	Construction dust and muddy water discharge was found at the site near Wan Chai Pier on 11 June 2018 afternoon.	ET confirmed with the Resident Site Staff that marine construction activity of removal of TWCR4 and stockpile of fill material at WCR3 Area were conducted under the Contractor of HK/2009/02 on 11 June 2018 afternoon. The Contractor of HK/2009/02 reported that double silt curtain was in place as mitigation measures during the marine activity and regular spraying water was provided as dust mitigation measures at WCR3 Area. Follow-up inspection was conducted on 28 June 2018, excavation works was observed at WCR3 Area and mitigation measures including watering during excavation was generally in place. Other dust mitigation measure includes covering the stockpile material and watering the dusty surface and haul road were generally in place. No particular dust impact was observed. No muddy water discharge or surface runoff related water quality monitoring impact was observed at Contract HK/2009/02 site area. Mitigation measures for marine activity includes providing double layers of silt curtain to enclose the marine activity area was generally in place and additional tarpaulin was provided to cover the temporary cut slope to avoid the potential surface runoff. In view of the public concern, the Contractor of HK/2009/02 was reminded to keep review the performance of dust mitigation measures including watering during excavation and material handling, covering the stockpile material and watering the dusty surface and haul road to avoid potential dust impact and minimize any potential dust impact to the surroundings. The Contractor of HK/2009/02 was also reminded to maintain regular checking on the embankment, silt curtain and tarpaulin condition to ensure no gap / void to avoid potential water quality related impact.	The interim report will be submitted to EPD on 4 July 2018. EPD advised no comment on 28 September 2018 on the interim investigation report and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
190116	12 January 2019	An EPD complaint was referred to the ET on 16 January 2019 (CASE Ref: H08/RS/00001 488-19, H08/RS/00001 532-19, and H08/RS/00001 663-19).	Victoria Harbour near Causeway Bay Typhoon Shelter	Milky water discharge was found at the Victoria Harbour, near Causeway Bay Typhoon Shelter on 12 January 2019	ET confirmed with the WDII Resident Site Staff that the concerned area was located out of the site area of Contract No. HK/2009/02 and the Contractor of HK/2009/02 had no activity at the area concerned on 12 January 2019. ET confirmed with the CWB Resident Site Staff that no construction works was conducted by the contractor of HY/2010/08 at Victoria Harbour, near Causeway Bay Typhoon Shelter on 12 January 2019 at around noon. Despite no construction activity was conducted under Contract HK/2009/02 and HY/2010/08 on the concerned date and location as confirmed with corresponding Resident Site Staff, in view of public concern, the Contractor of Contract HK/2009/02 and HY/2010/08 were reminded to review the on-site drainage system and the operation of wastewater treatment system. The Contractor of Contract HK/2009/02 and HY/2010/08 were also reminded to provide mitigation measure such as deployment of silt curtain to enclose the works area if any marine activity to be conducted at the concerned area.	The interim report will be submitted to EPD on 24 January 2019.





Appendix 10.1

**Construction Programme of Individual Contracts** 

	Activity Name	Ori Dur	Rem Dur	Scheduled /Actual Start	Scheduled / Actual Finish	Total Float	Calendar	Augu 05   12				eptember	22	2018
MONTHS R	OLLING PROGRAMME OF WORKS PROGRAMME REVIEWED 8 AUG	2018 (DD 7-9-18)						12	19	26	02 09	16	23	30
	TWCR4 AND CONSTRUCTION OF WCR4													
	ICR4 AND INSTALL SEAWALL													
A1000	TRANSPORT OF P5 FILL MATERIAL TO P34	10	10	30-Oct-18	08-Nov-18	32	HK Working Day							
MARINE EXCA							3,		-					
A1030	WEST SIDE EXC FOR G400 (1600M3) & 0.5T ARMOUR	20	20	07-Sep-18*	26-Sep-18	0	7-Day Workweek-1			++		·	WE	ST SIDE EX
A1040	ARRIVAL OF G400	1	1	17-Sep-18	17-Sep-18	143	7-Day Workweek-1		-				VAL OF G	400
A1050	ARRIVAL OF ARMOUR	1	1	21-Sep-18	22-Sep-18	134	HK Working Day					∽►∎	ARRIVAL	OFARMOL
<b>CUTTING D-W</b>	ALL													
A1080	EAST SIDE CORE HOLES	9	1	01-Sep-18 A	07-Sep-18	16	7-Day Workweek-1				EAST	SIDE CORE	HOLES	
A1090	WEST SIDE CORE HOLES	5	5	05-Sep-18 A	12-Sep-18	16	7-Day Workweek-1			;;;;;; <b>G</b>		WEST SIDE	CORE HC	JLES
A1100	VERTICAL CUT	20	5	05-Sep-18 A	11-Sep-18	13	7-Day Workweek-1			5		VERTICAL CU	JT	
A1110	HORIZONTAL CUT	20	20	07-Sep-18	26-Sep-18	5	7-Day Workweek-1				·••		🗖 но́	RIZONTÁL C
A1120	REMOVAL OF D-WALL	20	20	07-Sep-18	26-Sep-18	5	7-Day Workweek-1		-			÷		
INSTALL SEAV	VALL													
MANUFACTUR	E OF SEAWALL BLOCK													
A1125	MANUFACTURE OF SEAWALL BLOCK	86	43	27-Jul-18 A	19-Oct-18	40	7-Day Workweek-1	-						
A1127	MANUFACTURE OF FACING STONE	15	15	20-Oct-18	03-Nov-18	103	7-Day Workweek-1							
A1130	1ST DELVERY	1	1	13-Sep-18*	13-Sep-18	19	7-Day Workweek-1				E F	1ST DELIVE	ERY	
A1140	2ND DELIVERY	1	1	06-Oct-18*	06-Oct-18	9	7-Day Workweek-1							<b>--1</b> 21
A1150	3RD DELIVERY	1	1	12-Oct-18*	12-Oct-18	17	7-Day Workweek-1							
A1160	4TH DELVERY	1	1	19-Oct-18*	19-Oct-18	11	7-Day Workweek-1							
A1170	5TH DELIVERY	1	1	27-Oct-18*	27-Oct-18	4	7-Day Workweek-1		-					1
A1180	6TH DELNERY	1	1	02-Nov-18*	02-Nov-18	3	7-Day Workweek-1							
A1190	7TH DELNERY	1	1	09-Nov-18*	09-Nov-18	6	7-Day Workweek-1							
A1200	8TH DELIVERY	1	1	15-Nov-18*	15-Nov-18	14	7-Day Workweek-1							
INSTALLATION	OF EAST SIDE SEAWALL BLOCK			,										
A1210	MOUNTING ROCK BEDDING	6	6	19-Sep-18	24-Sep-18	19	7-Day Workweek-1					╘╼══		NTING ROCH
A1220	LEVELLING	3	3	25-Sep-18	27-Sep-18	19	7-Day Workweek-1		-			1	- <b>1</b>	EVELLING
A1230	M9 BLOCK	2	2	28-Sep-18	29-Sep-18	19	7-Day Workweek-1						<b>└</b> ► <u></u>	M9 BLOCK
A1240	LEVELLING	5	5	30-Sep-18	04-Oct-18	19	7-Day Workweek-1	1					<b>⊢</b>	
A1250	1ST LAYER OF BLOCK	4	4	05-Oct-18	08-Oct-18	19	7-Day Workweek-1							┕╺═
A1260	2ND LAYER	3	3	09-Oct-18	11-Oct-18	19	7-Day Workweek-1							►
A1270	3RD LAYER	3	3	12-Oct-18	14-Oct-18	19	7-Day Workweek-1							
A1280	4TH LAYER	3	3	15-Oct-18	17-Oct-18	19	7-Day Workweek-1							
A1290	5TH LAYER	3	3	18-Oct-18	20-Oct-18	19	7-Day Workweek-1							
A1300	6TH LAYER	3	3	21-Oct-18	23-Oct-18	19	7-Day Workweek-1							
A1310	TYPEA	4	4	24-Oct-18	27-Oct-18	19	7-Day Workweek-1							
A1320	GEOTEXTILE AND FILTER	4	4	28-Oct-18	31-Oct-18	19	7-Day Workweek-1							
A1330	B/F SOIL (5000m3)	8	8	01-Nov-18	08-Nov-18	19	7-Day Workweek-1							
A1340	PLACE CONC CUBES AND PARTLY B/F TO +3.5mPD (1000m3)	6	6	09-Nov-18	14-Nov-18	19	7-Day Workweek-1							
	OF WEST SIDE SEAWALL BLOCK			07 0 10									-	
A1370	MOUNTING ROCK BEDDING TYPE 12A & 12B	15	15	27-Sep-18	11-Oct-18	0	7-Day Workweek-1						-	
A1380	LEVELLING	4	4	12-Oct-18	15-Oct-18	0	7-Day Workweek-1							
A1390	M9 BLOCK	3	3	16-Oct-18	18-Oct-18	0	7-Day Workweek-1							
A1400	LEVELLING	7	7	19-Oct-18	25-Oct-18	0	7-Day Workweek-1							
A1410	1ST LAYER OF BLOCK	6	6	26-Oct-18	31-Oct-18	0	7-Day Workweek-1							
A1420	2ND LAYER	5	5	01-Nov-18	05-Nov-18	0	7-Day Workweek-1							
A1430	3RD LAYER 4TH LAYER	5	5	06-Nov-18	10-Nov-18	0	7-Day Workweek-1							
A1440	5TH LAYER	5	5	11-Nov-18	15-Nov-18	0	7-Day Workweek-1							
A1450		4	4	16-Nov-18	19-Nov-18	-	7-Day Workweek-1							
A1460	6TH LAYER	3	3	20-Nov-18	22-Nov-18	0	7-Day Workweek-1							
A1470 A1480	TYPEA	4	4	23-Nov-18	26-Nov-18	0	7-Day Workweek-1		1					
A1480	FLTER	4	4	27-Nov-18	30-Nov-18 06-Dec-18	0	7-Day Workweek-1		-					
A1490	B/F TO +2.8mPD	6	6	01-Dec-18		0	7-Day Workweek-1							

-	▼ Ivillesione			
•	<ul> <li>Critical Milestones</li> </ul>	<b>CHUN WO - CRGL</b>	CEDD CONTRACT NO. HK/2009/02	
	Current Works	JOINT VENTURE	WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)	
	Critical Works		3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)	
	-			
	Remaining Level of			

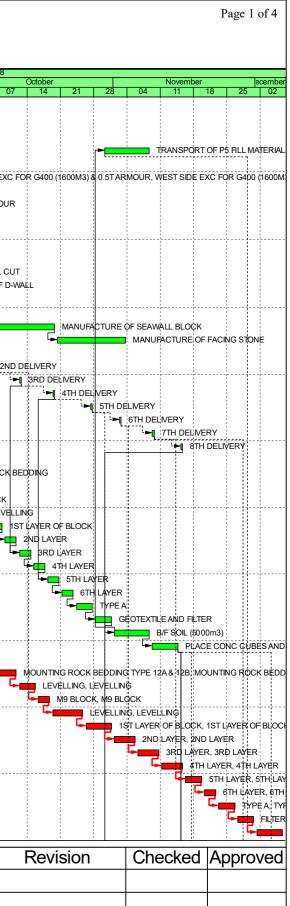




EAWALL NSTALL SEAWALL NSTALL SEAWALL SEAWALL DISMANTLE OLD SEAWALL BLOCK AND EXCAVATE ROCKFLL G400 LEVELLING IST LAYER OF SEAWALL BLOCK IST LAYER STD LAYER STD LAYER STD LAYER STT LAYER STT LAYER STT UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNITS SAY 1 CONCRETE		30 14 3 3 3 3 4 3 3 4 3 3 4 4 3 3 4 4 3 3 4 4 3 3 3 4 4 3 3 3 4 4 3 3 3 4 4 3 3 3 3 3 4 4 3 3 3 3 3 3 3 3 3 3 3 3 3		30-Nov-18 01-Nov-18 15-Nov-18 18-Nov-18 21-Nov-18 24-Nov-18 27-Nov-18 01-Dec-18 04-Dec-18 04-Dec-18 07-Sep-18* 21-Sep-18* 11-Oct-18 11-Oct-18 17-Nov-18	30-Dec-18 14-Nov-18 17-Nov-18 20-Nov-18 23-Nov-18 23-Nov-18 23-Nov-18 30-Nov-18 03-Dec-18 03-Dec-18 06-Dec-18 03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18 07-Sep-18	15 14 14 14 14 14 14 14 14 14 14 56 56 56 56 56 56 56	7-Day Workweek-1 7-Day Workweek-1		12 19				23 SAY 1 LOWE	ER BAY
NSTALL SEAWALL DISMANTLE OLD SEAWALL BLOCK AND EXCAVATE ROCKFLL G400 LEVELLING 1ST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 3RD LAYER 4TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5AY 1 LOWER 5AY 2 LOWER 5AY 2 LOWER 5AY 2 UPPER EAST COPING 5T UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS 5AY 1 FX REBAR		14 3 3 3 3 3 4 3 3 3 4 3 3 3 4 4 3 3 3 1 7 7 7 3 1 3 1 1 9	14 3 3 3 4 3 3 3 4 3 3 14 13 7 7 7 31 31	01-Nov-18 15-Nov-18 18-Nov-18 21-Nov-18 24-Nov-18 27-Nov-18 01-Dec-18 04-Dec-18 04-Dec-18 07-Sep-18* 21-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 11-Oct-18	14-Nov-18 17-Nov-18 20-Nov-18 23-Nov-18 26-Nov-18 30-Nov-18 03-Dec-18 06-Dec-18 20-Sep-18 03-Oct-18 10-Oct-18 10-Oct-18 17-Oct-18	14 14 14 14 14 14 14 14 14 14 14 56 56 56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1						ay 1 Lowe	
DISMANTLE OLD SEAWALL BLOCK AND EXCAVATE ROCKFILL G400 LEVELLING 1ST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5AY 2 LOWER 5AY 2 LOWER 5AY 2 UPPER EAST COPING 5T UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS 5AY 1 FX REBAR		14 3 3 3 3 3 4 3 3 3 4 3 3 3 4 4 3 3 3 1 7 7 7 3 1 3 1 1 9	14 3 3 3 4 3 3 3 4 3 3 14 13 7 7 7 31 31	01-Nov-18 15-Nov-18 18-Nov-18 21-Nov-18 24-Nov-18 27-Nov-18 01-Dec-18 04-Dec-18 04-Dec-18 07-Sep-18* 21-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 11-Oct-18	14-Nov-18 17-Nov-18 20-Nov-18 23-Nov-18 26-Nov-18 30-Nov-18 03-Dec-18 06-Dec-18 20-Sep-18 03-Oct-18 10-Oct-18 10-Oct-18 17-Oct-18	14 14 14 14 14 14 14 14 14 14 14 56 56 56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1						SAY 1 LOWE	
ROCKFILL G400 LEVELLING IST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5AY 1 LOWER BAY 1 LOWER BAY 2 LOWER BAY 2 LOWER BAY 2 UPPER EAST COPING 5T UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FX REBAR		3 3 3 4 3 3 3 3 3 3 1 4 3 3 7 7 7 3 1 3 1 1 9	3 3 3 4 3 3 3 14 13 7 7 31 31	15-Nov-18 18-Nov-18 21-Nov-18 24-Nov-18 01-Dec-18 04-Dec-18 07-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 11-Oct-18 17-Nov-18	17-Nov-18 20-Nov-18 23-Nov-18 26-Nov-18 30-Nov-18 03-Dec-18 06-Dec-18 20-Sep-18 03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	14 14 14 14 14 14 14 14 56 56 56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1						ay 1 Lowe	
ROCKFILL G400 LEVELLING IST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5AY 1 LOWER BAY 1 LOWER BAY 2 LOWER BAY 2 LOWER BAY 2 UPPER EAST COPING 5T UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FX REBAR		3 3 3 4 3 3 3 3 3 3 1 4 3 3 7 7 7 3 1 3 1 1 9	3 3 3 4 3 3 3 14 13 7 7 31 31	15-Nov-18 18-Nov-18 21-Nov-18 24-Nov-18 01-Dec-18 04-Dec-18 07-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 11-Oct-18 17-Nov-18	17-Nov-18 20-Nov-18 23-Nov-18 26-Nov-18 30-Nov-18 03-Dec-18 06-Dec-18 20-Sep-18 03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	14 14 14 14 14 14 14 14 56 56 56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1						ay 1 Lowe	
LEVELLING IST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5AY 1 LOWER 5AY 2 LOWER 5AY 2 LOWER 5AY 2 LOWER 5AY 2 UPPER 5AY 2 UPPER 5AST COPING 5T UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS 5AY 1 FIX REBAR		3 3 3 4 3 3 3 3 4 3 3 7 7 7 3 1 3 1 1 9	3 3 4 3 3 3 3 14 13 7 7 7 31	18-Nov-18 21-Nov-18 24-Nov-18 01-Dec-18 04-Dec-18 07-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 11-Oct-18	20-Nov-18 23-Nov-18 26-Nov-18 30-Nov-18 03-Dec-18 06-Dec-18 20-Sep-18 03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	14 14 14 14 14 14 14 56 56 56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1						ay 1 Lowe	
IST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5AY 1 LOWER 5AY 1 LOWER 5AY 2 LOWER 5AY 2 LOWER 5AY 2 UPPER 5AY 2 UPPER 5AST COPING 5T UNIT FOR BAY 12 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7		3 3 4 3 3 3 3 1 4 13 7 7 7 7 3 1 3 1 1 9	3 3 4 3 3 3 14 13 7 7 31 31	21-Nov-18 24-Nov-18 27-Nov-18 01-Dec-18 04-Dec-18 07-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 11-Oct-18	23-Nov-18 26-Nov-18 30-Nov-18 03-Dec-18 06-Dec-18 20-Sep-18 03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	14 14 14 14 14 56 56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1						AY 1 LOWE	
2ND LAYER 3RD LAYER 4TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TH LAYER 5TY 1 LOWER 5AY 1 LOWER 5AY 2 LOWER 5AY 2 LOWER 5AY 2 UPPER 5AY 1 DEPER 5AY 1		3 4 3 3 14 13 7 7 31 31 19	3 4 3 3 14 13 7 7 31 31	24-Nov-18 27-Nov-18 01-Dec-18 04-Dec-18 07-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 11-Oct-18	26-Nov-18 30-Nov-18 03-Dec-18 06-Dec-18 20-Sep-18 03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	14 14 14 14 56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1						ay 1 Lowe	
ATH LAYER ATH LAYER STH LAYER STH LAYER EAST OWER BAY 1 LOWER BAY 2 LOWER BAY 2 LOWER BAY 2 LOWER BAY 2 UPPER EAST COPING EAST COPING EA		4 3 3 14 13 7 7 31 31 1 9	4 3 3 14 13 7 7 31 31	27-Nov-18 01-Dec-18 04-Dec-18 07-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 17-Nov-18	30-Nov-18 03-Dec-18 06-Dec-18 20-Sep-18 03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	14 14 14 56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1						SAY 1 LOWE	
ATH LAYER STH LAYER STH LAYER BAY 1 LOWER BAY 1 LOWER BAY 2 LOWER BAY 2 LOWER BAY 2 LOWER BAY 2 LOWER BAY 1 UPPER EAST COPING EAST COPING		3 3 14 13 7 7 31 31 1 9	3 3 14 13 7 7 31 31	01-Dec-18 04-Dec-18 07-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 17-Nov-18	03-Dec-18 06-Dec-18 20-Sep-18 03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	14 14 56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1						ay 1 Lowe	
STH LAYER 57) BAY 1 LOWER BAY 2 LOWER BAY 2 LOWER BAY 2 UPPER EAST COPING EAST COPING ST UNIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		3 14 13 7 7 31 31 1 19	3 14 13 7 7 31 31	04-Dec-18 07-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 17-Nov-18	06-Dec-18 20-Sep-18 03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	14 56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1						ay 1 Lowe	
E 7) BAY 1 LOWER BAY 2 LOWER BAY 2 LOWER BAY 2 UPPER EAST COPING EAST COPING EAST COPING EAST COPING EAST LINIT FOR BAY 12 RECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		14 13 7 7 31 1 19	14 13 7 7 31 31	07-Sep-18* 21-Sep-18 04-Oct-18 11-Oct-18 17-Nov-18	20-Sep-18 03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	56 56 56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1						BAY 1 LOWE	
BAY 1 LOWER BAY 2 LOWER BAY 1 UPPER BAY 2 UPPER EAST COPING EAST COPING ARRMAL OF PRECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		13 7 7 31 1 19	13 7 7 31 1	21-Sep-18 04-Oct-18 11-Oct-18 17-Nov-18	03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	56 56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1						ay 1 Lowe	
BAY 1 LOWER BAY 2 LOWER BAY 1 UPPER BAY 2 UPPER EAST COPING EAST COPING ARRMAL OF PRECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		13 7 7 31 1 19	13 7 7 31 1	21-Sep-18 04-Oct-18 11-Oct-18 17-Nov-18	03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	56 56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1						ay 1 Lowe	
BAY 2 LOWER BAY 1 UPPER BAY 2 UPPER EAST COPING EAST COPING ARRIVAL OF PRECAST UNIT FOR BAY 12 RECAST UNIT RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		13 7 7 31 1 19	13 7 7 31 1	21-Sep-18 04-Oct-18 11-Oct-18 17-Nov-18	03-Oct-18 10-Oct-18 17-Oct-18 17-Dec-18	56 56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1						SAY 1 LOWE	
BAY 1 UPPER BAY 2 UPPER EAST COPING EAST COPING ARRIVAL OF PRECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		7 7 31 1 19	7 7 31 1	04-Oct-18 11-Oct-18 17-Nov-18	10-Oct-18 17-Oct-18 17-Dec-18	56 56 39	7-Day Workweek-1 7-Day Workweek-1 7-Day Workweek-1							BA1
BAY 2 UPPER EAST COPING ST UNIT FOR BAY 12 ARRIVAL OF PRECAST UNIT FOR BAY 12 RECAST UNIT INSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		7 31 1 19	7 31 1	11-Oct-18 17-Nov-18	17-Oct-18 17-Dec-18	56 39	7-Day Workweek-1 7-Day Workweek-1							
EAST COPING T UNIT FOR BAY 12 ARRIVAL OF PRECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		31 1 19	31	17-Nov-18	17-Dec-18	39	7-Day Workweek-1						1         3           2         3           3         3           4         3           5         3           6         3           7         3           8         3           9         3           1         3           1         3           2         3           3         3           3         3	
ARRIVAL OF PRECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		1 19	1											
ARRIVAL OF PRECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		1 19	1										1 8 1 8 1 8 1 8 1 8 1 8 1 8	
ARRIVAL OF PRECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		19		07-Sep-18*	07-Sep-18	62	7-Day Workwook 1						1	
ARRIVAL OF PRECAST UNIT FOR BAY 12 RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		19		07-Sep-18*	07-Sep-18	62	7-Day Workweek 1						. i	
RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		19		07-Sep-18*	07-Sep-18	62	7-Day Workwook 1						LL       	
RECAST UNIT NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR		19					- Day WURWCCA-I	1	1			NAL OF PREC	CASTUNITE	FOR BA
NSTALLATION OF PRECAST UNITS BAY 1 FIX REBAR							,				1			
BAY 1 FIX REBAR			19	25-Oct-18	13-Nov-18	15	7-Day Workweek-1							
			2	01-Nov-18	03-Nov-18		•							
DATICONCRETE			1			15	7-Day Workweek-1							
		1		03-Nov-18	04-Nov-18	15	7-Day Workweek-1							-
BAY 2 FIX REBAR		2	2	06-Nov-18	08-Nov-18	15	7-Day Workweek-1							
BAY 2 CONCRETE		1	1	08-Nov-18	09-Nov-18	15	7-Day Workweek-1		1					
														į
		13	13	17-Nov-18	30-Nov-18	15	7-Day Workweek-1							
BAY 19 STEEL BULKHEAD		2	0	01-Sep-18 A	05-Sep-18 A		7-Day Workweek-1							
		5	1	04-Sep-18 A	08-Sep-18	15	7-Day Workweek-1			<b> ►[</b>	BAY			
CONSTRUCTION OF EARTH PLATFORM		6	6	08-Sep-18	14-Sep-18	15	7-Day Workweek-1						UCTION OF	EARTH
DUTING														
WEST SIDE PIPE PILING		10	3	01-Aug-18 A	09-Sep-18	17	7-Day Workweek-1				w	EST SIDE PIP	E PILING	
WEST SIDE GROUTING		22	15	21-Aug-18 A	22-Sep-18	146	7-Day Workweek-1	-	<b>&gt;</b>	1 1			WEST SID	E GROL
EAST SIDE PIPE PILING		13	13	11-Sep-18	24-Sep-18	15	7-Day Workweek-1				╘╸		EAST S	1
EAST SIDE GROUTING		11	11	20-Sep-18	01-Oct-18	15	7-Day Workweek-1					· · · •		EAST
S														
DEMOLISH OLD CULVERT, CUT STEEL PILE AND INSTALL ELS		10	10	21-Sep-18	01-Oct-18	15	7-Day Workweek-1							DEMO
EXCAVATE TP -2.9mPD		8	8	01-Oct-18	09-Oct-18	15	7-Day Workweek-1							_
B/F G200 & ELS		8	8	09-Oct-18	17-Oct-18	15	7-Day Workweek-1							C
TAMPING		2	2	17-Oct-18	19-Oct-18	15	7-Day Workweek-1							·
LEVELLING		5	5	19-Oct-18	24-Oct-18	15	7-Day Workweek-1	-	1					
														Ì
									1					
					-			·	f					
				-								ZONE B		
ZONE C		14	14	17-Nov-18	30-Nov-18	44	7-Day Workweek-1							
ZONEA		5	0	17-Aug-18 A	30-Aug-18 A		7-Day Workweek-1			ZONE	EA			
ZONE B		7	7	11-Sep-18	18-Sep-18	149	7-Day Workweek-1				¦► <mark>⊂</mark>	ZON	NE B	
ne													Dal	<u> </u>
					CONTO			0000	100					T
Milestones   CHUN WO - CKGL				CEDD	CONTR	AUI	NU. HK/	2009/	/02					-+
	יו מעע	<u>^</u> -	n+		hai D.		at Man C	ha: r		Contr	+ -)	<b>۱</b>		
	BAY 3 FX REBAR BAY 3 FX REBAR BAY 3 CONCRETE CLEAN UP, W/P AND B/F BAY 12 EAD BAY 19 STEEL BULKHEAD BAY 13 CONCRETE BULKHEAD CONSTRUCTION OF EARTH PLATFORM OUTING WEST SIDE PIPE PILING WEST SIDE PIPE PILING WEST SIDE GROUTING EAST SDE PIPE PILING EAST SDE PIPE PILING EAST SDE PIPE PILING EAST SDE PIPE PILING EAST SDE GROUTING EAST SDE GROUTING EAST SDE GROUTING EAST SDE PIPE PILING EAST SDE GROUTING EAST SDE PIPE PILING EAST SDE GROUTING EAST SDE PIPE PILING EAST SDE GROUTING EAST SDE GROUTING EAST SDE GROUTING EAST SDE PIPE PILING EAST SDE GROUTING EAST SDE GROUTING SDE GROUTING EAST SDE G	BAY 3 FIX REBAR BAY 3 CONCRETE CLEAN UP, WP AND BF BAY 12 EAD BAY 19 STEEL BULKHEAD BAY 19 STEEL BULKHEAD BAY 13 CONCRETE BULKHEAD CONSTRUCTION OF EARTH PLATFORM OUTING WEST SIDE PIPE PLING WEST SIDE GROUTING EAST SIDE GROUTING EAST SIDE GROUTING S DEMOLISH OLD CULVERT, CUT STEEL PLE AND INSTALL ELS EXCAVATE TP -2.9mPD BF G200 & ELS TAMPING LEVELLING LTO +1.5mPD ZONE A ZONE A ZONE A ZONE A ZONE A ZONE B TME Milestones t Works CHUN WO - CRGL JOINT VENTURE WD II -	BAY 3 FIX REBAR 2 BAY 3 FIX REBAR 1 BAY 12 EAD EAD EAD BAY 12 EAD BAY 13 STEEL BULKHEAD BAY 19 STEEL BULKHEAD CONSTRUCTION OF EARTH PLATFORM DUTING WEST SIDE PIPE PLLING WEST SIDE GROUTING EAST SIDE GROUTING EAST SIDE GROUTING EAST SIDE GROUTING BIF G200 & ELS TAMPING LEVELLING CONSTRUCTOR OF EARTH PLATFORM DEMOLISH OLD CULVERT, CUT STEEL PILE AND INSTALL ELS 10 EXCAVATE TP -2.9mPD BIF G200 & ELS TAMPING LEVELLING CHUN WO - CRGL JOINT VENTURE WD II - CE	BAY 3 FIX REBAR     2     2       BAY 3 FIX REBAR     1     1       CLEAN UP, WIP AND BJF     13     13       BAY 12     EAD     2     0       BAY 13 CONCRETE BULKHEAD     2     0       BAY 13 CONCRETE BULKHEAD     2     0       CONSTRUCTION OF EARTH PLATFORM     6     6       DUTING     10     3       WEST SIDE PIPE PLING     10     3       EAST SIDE PIPE PLING     10     13       EAST SIDE PIPE PLING     10     11       S     11     11       S     10     10       EXCAVATE TP -2.9mPD     8     8       BIF G200 & ELS     8     8       EXCAVATE TP -2.9mPD     8     8       DEMOLISH OLD CULVERT, CUTSTEEL PLE AND INSTALL ELS     10     10       EXCAVATE TP -2.9mPD     8     8       BIF G200 & ELS     8     8       IEVELING     2     2       LEVELING     5     5       CNEA     21     0       ZONEA     5     0       ZONE A     5     0       ZONE A     5     0       ZONE B     7     7       MILESTONES     CHUN WO - CRGL     WD II - CENTRA   <	BAY 3 FIX REBAR       2       2       13 Nov-18         BAY 3 CONCRETE       1       1       15 Nov-18         CLEAN UP, WIP AND B/F       13       13       17 Nov-18         EAD       EAD       2       0       01-Sep-18A         BAY 13 CONCRETE       0       5       1       04-Sep-18A         CONSTRUCTION OF EARTH PLATFORM       6       6       08-Sep-18         DUTINO       10       3       01-Aug-18A         WEST SDE PPE PLING       10       3       01-Aug-18A         WEST SDE GROUTING       10       3       01-Aug-18A         WEST SDE GROUTING       10       1       11       120-Sep-18         S       10       10       21       13       13       11       120-Sep-18         S       10       10       21       13       13       11       120-Sep-18         DEMOLISH OLD CULVERT, CUTSTEEL PLIE AND INSTALL ELS       10       10       21-Sep-18       10       10       21-Sep-18         S       S       10       10       21-Sep-18       10       10       21-Sep-18         EXCAMARE TP -2.9mPD       8       8       09-Oct-18       8       6       0-	BAY 3 FIX REBAR     2     2     13 Alou-18     15 Alou-18     15 Alou-18     15 Alou-18     15 Alou-18     16 Alou-18       BAY 12     1     1     17 Alou-18     10 Alou-18     16 Alou-18     10 Alou-18     05 Sep-18A     05 Sep-18A     05 Sep-18A     05 Sep-18A     06 Sep-18     08 Sep-18     14 Sep-18     00 Sep-18     08 Sep-18     01 Alou-18     08 Alou-18     01 Alou-18     02 Alou-18     01 Alou-18     02 Alou-18     01 Alou-18 <td< td=""><td>BAY 3 FIX REBAR     2     2     13-Nov-18     15-Nov-18     15       BAY 3 CONCRETE     1     1     15-Nov-18     16     15       BAY 12     2     0     01-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     06-Sep-18A     06-Sep-18A     06-Sep-18A     06-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     06-Sep-18A     17       VISTOR     0     0     0     0.1-Aug-18A     06-Sep-18A     17     06-Sep-18A     16-Sep-18A     10-Ou-18<!--</td--><td>BAY 3 FOR REBAR       2       2       1 3 Non-18       15 Non-18       15 7 Jay Workweek.1         BAY 3 CONCRETE       1 1       1 1 1       15 Non-18       16 Non-18       16 Non-18       15 7 Jay Workweek.1         EAV 3 CONCRETE       1 3 1 7 Non-18       30 Non-18       15 7 Jay Workweek.1       15 7 Jay Workweek.1         EAV 12       2       0       01-Sep-18A       05-Sep-18       7 Jay Workweek.1         EAV 13 STELL BULKHEAD       2       0       01-Sep-18A       05-Sep-18       15 7 Jay Workweek.1         CONSTRUCTOR OF EARTH PLATFORM       6       6       08-Sep-18       14 Sep-18       15 7 Jay Workweek.1         DUTING       1       3       01-Aug-18A       09-Sep-18       15 7 Jay Workweek.1         DUTING       2       10       3       01-Aug-18A       09-Sep-18       15 7 Jay Workweek.1         DUTING       2       1       11 11       20-Sep-18       10 Jay 24 Sep-18       15 7 Jay Workweek.1         SOCOUTING       2       1       14 Jay 11 Jay 24 Sep-18       10 Jay 18 Jay 24 Sep-18       15 7 Jay Workweek.1         SOCOUTING       3       01-Aug-18 A       09-Sep-18       15 7 Jay Workweek.1       15 7 Jay Workweek.1         SOCOUTING       2       2 Jay 17 Ja</td><td>BAY 3FM REBAR       2       2       13 Avoi 18       15 Nov-18       15       7-Day Wokweek-1         BAY 3CONCRETE       1       1       15 Nov-18       16 Nov-18       15       7-Day Wokweek-1         BAY 3CONCRETE       1       1       15 Nov-18       16 Nov-18       15       7-Day Wokweek-1         EAV 12       Vector       &lt;</td><td>BW 3 EN REBAR       2       2       1       15 Avon-18       15       7-Day Workweek-1         BW 3 CONCRETE       1       1       15       15       7-Day Workweek-1         BW 3 CONCRETE       1       1       15       15       7-Day Workweek-1         BW 12      </td><td>BW 3 ERBAR       2       2       1       13-Nor-18       15       7-Day Wokweek1         M 3 BW 3 CONCRETE       13       13       13       13       13       14-Nor-18       15       7-Day Wokweek1         CLEAN UP WP AND BF       13       13       13       17-Abex18       30-Nor-18       15       7-Day Wokweek1         BM 12 STELE BULKHEAD       2       0       01-Sep-18A       05-Sep-18A       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       0       01-Sep-18A       05-Sep-18       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       0       01-Sep-18A       05-Sep-18       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       0       01-Sep-18A       09-Sep-18       14       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       10       13       01-Sep-18       15       7-Day Wokweek1         DUING       13       13       11-Sep-18       15       7-Day Wokweek1       16       7-Day Wokweek1         DUING       13       13       13       13       15       7-Day Wokweek1       16       7-Day Wokweek1         DUING       11       11       24-Sep-18<td>BAY 3 BY REFAR       2       2       2       1 Shou-18       15       7Day Woksweek1         BAY 3 CONCRETE       1       1 Shou-18       16 Nou-18       15       7Day Woksweek1         CLEN UP, WP AND BF       13       13       17 Nou-18       30Nucr48       15       7Day Woksweek1         RAY 12      </td><td>BAY 3 FREAR       2       2       2       2       1       1 Shuoria       15       72ay Wokweeki         BAY 3 GONCREE       1       1       1 Shuoria       15       72ay Wokweeki       1         BAY 3 GONCREE       13       13       13       13       17 Nov-18       30 Nov-18       15       72ay Wokweeki         BAY 32       Check       5       0       01Sept 18       05Sept 18A       72ay Wokweeki       1</td><td>BW 3 EREAR       2       2       2       15 Mon-18       16 Korb       17 Korb       16 Korb       17 Korb       16 K</td></td></td></td<>	BAY 3 FIX REBAR     2     2     13-Nov-18     15-Nov-18     15       BAY 3 CONCRETE     1     1     15-Nov-18     16     15       BAY 12     2     0     01-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     06-Sep-18A     06-Sep-18A     06-Sep-18A     06-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     05-Sep-18A     06-Sep-18A     17       VISTOR     0     0     0     0.1-Aug-18A     06-Sep-18A     17     06-Sep-18A     16-Sep-18A     10-Ou-18 </td <td>BAY 3 FOR REBAR       2       2       1 3 Non-18       15 Non-18       15 7 Jay Workweek.1         BAY 3 CONCRETE       1 1       1 1 1       15 Non-18       16 Non-18       16 Non-18       15 7 Jay Workweek.1         EAV 3 CONCRETE       1 3 1 7 Non-18       30 Non-18       15 7 Jay Workweek.1       15 7 Jay Workweek.1         EAV 12       2       0       01-Sep-18A       05-Sep-18       7 Jay Workweek.1         EAV 13 STELL BULKHEAD       2       0       01-Sep-18A       05-Sep-18       15 7 Jay Workweek.1         CONSTRUCTOR OF EARTH PLATFORM       6       6       08-Sep-18       14 Sep-18       15 7 Jay Workweek.1         DUTING       1       3       01-Aug-18A       09-Sep-18       15 7 Jay Workweek.1         DUTING       2       10       3       01-Aug-18A       09-Sep-18       15 7 Jay Workweek.1         DUTING       2       1       11 11       20-Sep-18       10 Jay 24 Sep-18       15 7 Jay Workweek.1         SOCOUTING       2       1       14 Jay 11 Jay 24 Sep-18       10 Jay 18 Jay 24 Sep-18       15 7 Jay Workweek.1         SOCOUTING       3       01-Aug-18 A       09-Sep-18       15 7 Jay Workweek.1       15 7 Jay Workweek.1         SOCOUTING       2       2 Jay 17 Ja</td> <td>BAY 3FM REBAR       2       2       13 Avoi 18       15 Nov-18       15       7-Day Wokweek-1         BAY 3CONCRETE       1       1       15 Nov-18       16 Nov-18       15       7-Day Wokweek-1         BAY 3CONCRETE       1       1       15 Nov-18       16 Nov-18       15       7-Day Wokweek-1         EAV 12       Vector       &lt;</td> <td>BW 3 EN REBAR       2       2       1       15 Avon-18       15       7-Day Workweek-1         BW 3 CONCRETE       1       1       15       15       7-Day Workweek-1         BW 3 CONCRETE       1       1       15       15       7-Day Workweek-1         BW 12      </td> <td>BW 3 ERBAR       2       2       1       13-Nor-18       15       7-Day Wokweek1         M 3 BW 3 CONCRETE       13       13       13       13       13       14-Nor-18       15       7-Day Wokweek1         CLEAN UP WP AND BF       13       13       13       17-Abex18       30-Nor-18       15       7-Day Wokweek1         BM 12 STELE BULKHEAD       2       0       01-Sep-18A       05-Sep-18A       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       0       01-Sep-18A       05-Sep-18       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       0       01-Sep-18A       05-Sep-18       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       0       01-Sep-18A       09-Sep-18       14       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       10       13       01-Sep-18       15       7-Day Wokweek1         DUING       13       13       11-Sep-18       15       7-Day Wokweek1       16       7-Day Wokweek1         DUING       13       13       13       13       15       7-Day Wokweek1       16       7-Day Wokweek1         DUING       11       11       24-Sep-18<td>BAY 3 BY REFAR       2       2       2       1 Shou-18       15       7Day Woksweek1         BAY 3 CONCRETE       1       1 Shou-18       16 Nou-18       15       7Day Woksweek1         CLEN UP, WP AND BF       13       13       17 Nou-18       30Nucr48       15       7Day Woksweek1         RAY 12      </td><td>BAY 3 FREAR       2       2       2       2       1       1 Shuoria       15       72ay Wokweeki         BAY 3 GONCREE       1       1       1 Shuoria       15       72ay Wokweeki       1         BAY 3 GONCREE       13       13       13       13       17 Nov-18       30 Nov-18       15       72ay Wokweeki         BAY 32       Check       5       0       01Sept 18       05Sept 18A       72ay Wokweeki       1</td><td>BW 3 EREAR       2       2       2       15 Mon-18       16 Korb       17 Korb       16 Korb       17 Korb       16 K</td></td>	BAY 3 FOR REBAR       2       2       1 3 Non-18       15 Non-18       15 7 Jay Workweek.1         BAY 3 CONCRETE       1 1       1 1 1       15 Non-18       16 Non-18       16 Non-18       15 7 Jay Workweek.1         EAV 3 CONCRETE       1 3 1 7 Non-18       30 Non-18       15 7 Jay Workweek.1       15 7 Jay Workweek.1         EAV 12       2       0       01-Sep-18A       05-Sep-18       7 Jay Workweek.1         EAV 13 STELL BULKHEAD       2       0       01-Sep-18A       05-Sep-18       15 7 Jay Workweek.1         CONSTRUCTOR OF EARTH PLATFORM       6       6       08-Sep-18       14 Sep-18       15 7 Jay Workweek.1         DUTING       1       3       01-Aug-18A       09-Sep-18       15 7 Jay Workweek.1         DUTING       2       10       3       01-Aug-18A       09-Sep-18       15 7 Jay Workweek.1         DUTING       2       1       11 11       20-Sep-18       10 Jay 24 Sep-18       15 7 Jay Workweek.1         SOCOUTING       2       1       14 Jay 11 Jay 24 Sep-18       10 Jay 18 Jay 24 Sep-18       15 7 Jay Workweek.1         SOCOUTING       3       01-Aug-18 A       09-Sep-18       15 7 Jay Workweek.1       15 7 Jay Workweek.1         SOCOUTING       2       2 Jay 17 Ja	BAY 3FM REBAR       2       2       13 Avoi 18       15 Nov-18       15       7-Day Wokweek-1         BAY 3CONCRETE       1       1       15 Nov-18       16 Nov-18       15       7-Day Wokweek-1         BAY 3CONCRETE       1       1       15 Nov-18       16 Nov-18       15       7-Day Wokweek-1         EAV 12       Vector       <	BW 3 EN REBAR       2       2       1       15 Avon-18       15       7-Day Workweek-1         BW 3 CONCRETE       1       1       15       15       7-Day Workweek-1         BW 3 CONCRETE       1       1       15       15       7-Day Workweek-1         BW 12	BW 3 ERBAR       2       2       1       13-Nor-18       15       7-Day Wokweek1         M 3 BW 3 CONCRETE       13       13       13       13       13       14-Nor-18       15       7-Day Wokweek1         CLEAN UP WP AND BF       13       13       13       17-Abex18       30-Nor-18       15       7-Day Wokweek1         BM 12 STELE BULKHEAD       2       0       01-Sep-18A       05-Sep-18A       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       0       01-Sep-18A       05-Sep-18       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       0       01-Sep-18A       05-Sep-18       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       0       01-Sep-18A       09-Sep-18       14       15       7-Day Wokweek1         BW 13 STELE BULKHEAD       2       10       13       01-Sep-18       15       7-Day Wokweek1         DUING       13       13       11-Sep-18       15       7-Day Wokweek1       16       7-Day Wokweek1         DUING       13       13       13       13       15       7-Day Wokweek1       16       7-Day Wokweek1         DUING       11       11       24-Sep-18 <td>BAY 3 BY REFAR       2       2       2       1 Shou-18       15       7Day Woksweek1         BAY 3 CONCRETE       1       1 Shou-18       16 Nou-18       15       7Day Woksweek1         CLEN UP, WP AND BF       13       13       17 Nou-18       30Nucr48       15       7Day Woksweek1         RAY 12      </td> <td>BAY 3 FREAR       2       2       2       2       1       1 Shuoria       15       72ay Wokweeki         BAY 3 GONCREE       1       1       1 Shuoria       15       72ay Wokweeki       1         BAY 3 GONCREE       13       13       13       13       17 Nov-18       30 Nov-18       15       72ay Wokweeki         BAY 32       Check       5       0       01Sept 18       05Sept 18A       72ay Wokweeki       1</td> <td>BW 3 EREAR       2       2       2       15 Mon-18       16 Korb       17 Korb       16 Korb       17 Korb       16 K</td>	BAY 3 BY REFAR       2       2       2       1 Shou-18       15       7Day Woksweek1         BAY 3 CONCRETE       1       1 Shou-18       16 Nou-18       15       7Day Woksweek1         CLEN UP, WP AND BF       13       13       17 Nou-18       30Nucr48       15       7Day Woksweek1         RAY 12	BAY 3 FREAR       2       2       2       2       1       1 Shuoria       15       72ay Wokweeki         BAY 3 GONCREE       1       1       1 Shuoria       15       72ay Wokweeki       1         BAY 3 GONCREE       13       13       13       13       17 Nov-18       30 Nov-18       15       72ay Wokweeki         BAY 32       Check       5       0       01Sept 18       05Sept 18A       72ay Wokweeki       1	BW 3 EREAR       2       2       2       15 Mon-18       16 Korb       17 Korb       16 Korb       17 Korb       16 K


3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)

Remaining Level of...

**Critical Works** 

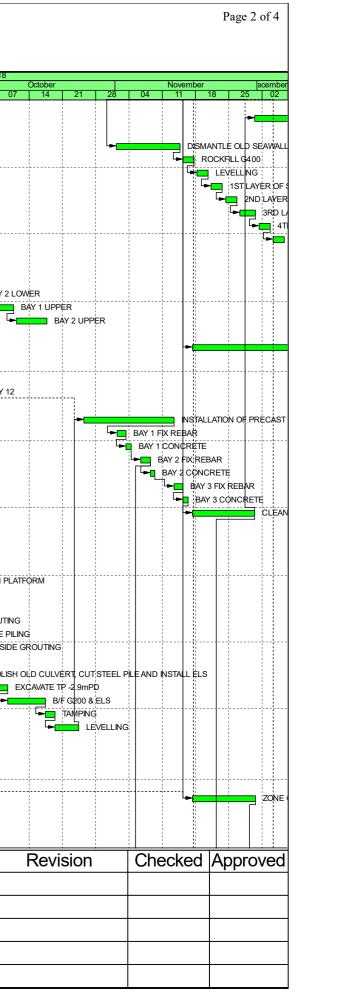

ctivity ID	Activity Name		Ori Dur	Rem Dur	Scheduled /Actual Start	Scheduled / Actual Finish	Total Float	Calendar		gust				ptember		20	18
40110									05 1	2 1	9 2	6 0	2 09	16	23	30	07
A2110	ZONE C		5	5	01-Dec-18	05-Dec-18	71	7-Day Workweek-1				-		1 1 1			
MANHOLE										-	-			-			
A2130	MH7352A		8	6	05-Sep-18 A	12-Sep-18	106	7-Day Workweek-1						MH7352A	111705497		
A2140	MH7354&7355		10	7	05-Sep-18 A	19-Sep-18	106	7-Day Workweek-1				-			/H7354&73	эээ MH7341	
A2150	MH7341		9	9	19-Sep-18	28-Sep-18	106	7-Day Workweek-1								NIT / 34 I	
DRAOMAGE																	
CH3730-3760													01417054	TOROY			
A2200	375MM DRAIN FROM SMH7354	IO BOX	16	0	31-Jul-18 A	18-Aug-18 A	40	7-Day Workweek-1					SMH7354		265 TO 726		
A2210	375M SMH7355 TO 7354		13	4	20-Aug-18 A	10-Sep-18	16	7-Day Workweek-1			1	Ļ		5M \$MH73	200 MM		. то <sup>.</sup>
A2220	300MM SMH734F1 TO 7355		11	10	03-Sep-18 A	21-Sep-18	16	7-Day Workweek-1							300MM S	L L	
A2230	BACKFILLING		13	13	21-Sep-18	04-Oct-18	16	7-Day Workweek-1		-	-			-	<u>:</u> Г		ACK
A2240	AIR TEST AND CCTV		3	3	04-Oct-18	07-Oct-18	16	7-Day Workweek-1							i F		AIF
BCO A2250	600MM DRAIN SMH7352A TO BC	NY .	11	0	30-Jul-18 A	09-Aug-18 A		7 Doy Workwook 1	600MA		SMH7352						
A2260		*	8	8	07-Nov-18	-	22	7-Day Workweek-1			511117 552	X 10 DO					
	BAY 12 (1200MM TO BOX)		-	-		15-Nov-18	22	7-Day Workweek-1								·	
A2270 CH3730-3760 REM	BAY 12 TO 14 GULLIES AND 225	DRAIN	12	12	24-Nov-18	06-Dec-18	22	7-Day Workweek-1		-	-	-					
A2280	300MM DRAIN SMH7341 TO 735	2		0	06-Dec-18	15-Dec-18	22	7 Dev Wedeveek 1				-		-			
	300MIN DRAIN SMH7341 10 735	3	9	9	06-Dec-18	15-Dec-16	22	7-Day Workweek-1				1					
ROADWORK												-					
HHR	BOAD FORMATION		i	10	00.0 10	40.0 / 10	10	7.0									
A2390	ROAD FORMATION		12	12	30-Sep-18	12-Oct-18	16	7-Day Workweek-1				1			-	;	Г
A2400	TESTING		10	10	12-Oct-18	22-Oct-18	16	7-Day Workweek-1		-							4
A2410	KERB		8	8	22-Oct-18	30-Oct-18	16	7-Day Workweek-1		-	-	1					
A2420	SUB-BASE		12	12	30-Oct-18	11-Nov-18	16	7-Day Workweek-1						-			
A2430	TEST		8	8	11-Nov-18	19-Nov-18	16	7-Day Workweek-1									
A2440	ROAD FORMATION		3	3	19-Nov-18	22-Nov-18	16	7-Day Workweek-1				-					
A2450	TEST AND SUB-BASE		11	11	22-Nov-18	03-Dec-18	16	7-Day Workweek-1									
A2460	ROAD FURNITURE		14	14	28-Nov-18	12-Dec-18	16	7-Day Workweek-1		-	-	1					
A2470	BLACK TOP		9	9	03-Dec-18	12-Dec-18	16	7-Day Workweek-1				-		-			
600mm Sewere																	
FIRST STAGE																	
A2500	600MM SEWER		5	1	26-Jul-18 A	07-Sep-18	97	7-Day Workweek-1					600MN	N SEWER		1	
A2510	B/F		5	5	08-Sep-18	12-Sep-18	97	7-Day Workweek-1		-	-	1	<b>F</b>	B/F			
A2520	SUB-BASE		9	9	13-Sep-18	21-Sep-18	97	7-Day Workweek-1					<b>-</b>	<u> </u>	SUB-BAS	Æ	
A2530	BLACKTOP		2	2	22-Sep-18	23-Sep-18	97	7-Day Workweek-1			-	-			BLACK	TOP	
A2540	TTA		1	1	24-Sep-18	24-Sep-18	97	7-Day Workweek-1					-		ττα		
SECOND STAGE												-			ſ.		
A2550	600MM SEWER		12	12	25-Sep-18	06-Oct-18	97	7-Day Workweek-1			-	1					600
A2560	B/F		5	5	07-Oct-18	11-Oct-18	97	7-Day Workweek-1		-						5	
A2570	SUB-BASE		9	9	12-Oct-18	20-Oct-18	97	7-Day Workweek-1				-					G
A2580	BLACKTOP		2	2	21-Oct-18	22-Oct-18	97	7-Day Workweek-1									
A2590	TTA		1	1	23-Oct-18	23-Oct-18	97	7-Day Workweek-1				1					
FINAL STAGE																	
A2600	600MM SEWER mh4.13 TO 4.15	TO 4.17	11	11	24-Oct-18	03-Nov-18	97	7-Day Workweek-1		-							
A2610	AIR TEST		1	1	04-Nov-18	04-Nov-18	97	7-Day Workweek-1									
A2620	b/f		3	3	05-Nov-18	07-Nov-18	97	7-Day Workweek-1								;;	
A2630	AIR TEST AND CCTV		2	2	08-Nov-18	09-Nov-18	97	7-Day Workweek-1				1					
	/CR1 & WCR3 REMAINING W	NORKS		-	00110110	00110110	0.	1 Buy Hondrook 1						-			
		VUKNO			00.1.1.40.4	00.0 40	101	70 11 14					CMC				
A2650	CMS INSTALLATION		11	1	28-Jul-18 A	08-Sep-18	101	7-Day Workweek-1						INSTALLAT	IUN	;	
A2660	WCR1 U CHANNELS		50	50	07-Sep-18*	26-Oct-18	52	7-Day Workweek-1								EVDO E	D. (5
A2670	EXPO DRIVE COVER REMEDIAL		46	23	15-Aug-18 A	29-Sep-18	123	7-Day Workweek-1				1		[:		EXPO D	RIVE
A2680	EXPO DRIVE COPING		28	28	17-Sep-18	14-Oct-18	123	7-Day Workweek-1				1		* <b></b>			
A2690	WCR1 EVA		59	59	01-Nov-18*	29-Dec-18	47	7-Day Workweek-1				1		-			
A2700	WCR3 SUB-BASE		24	24	17-Nov-18*	10-Dec-18	61	7-Day Workweek-1				-				1	
A2710	REPAIR COPING		11	11	29-Nov-18*	09-Dec-18	67	7-Day Workweek-1									
	4														Da	ite	
<ul> <li>Miles</li> </ul>	sione															<u> </u>	
A O	ol Milesteres	CHUN WO - CRGL			CEDD		2ACT	<sup>-</sup> NO. HK/2	2000	02							
<ul> <li>Critic</li> </ul>	cal Milestones				CLDD	CONTR		NO. 117/2	2003/	υz							
<b>^</b>		JOINT VENTURE	WD II - Ce	ntr	al Wand	hai Rv	nass	at Wan C	hai F	ast	(Co	ntra	ct 2				
	ent Works						-				-		-			-+	
			3-MON	TH	ROLLIN	IG PRO	GRA	AMME (da	ta da	te O	7-Se	ep-1	8)				
	cal Works						v						-,				
- Dave	aining Level of															-+	

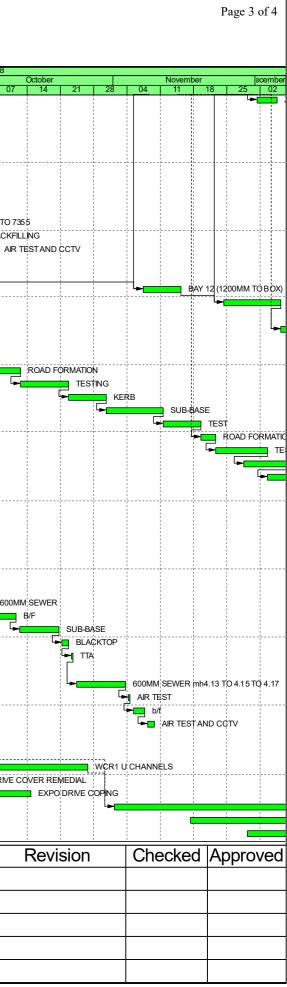


Activity ID	Activity Name	Ori	Rem	Scheduled	Scheduled /	Total	Calendar									20	)18								
		Dur	Dur	/Actual Start	Actual Finish	Float			August				Sept	ember				October				Novemb	er	e	embe
								05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02
A2720	WCR1&3 ARMOUR SLOPE PROFILE	31	31	01-Dec-18*	31-Dec-18	45	7-Day Workweek-1																	ſ	
A2740	REINSTATE WCR3 EXIT	23	23	24-Sep-18*	16-Oct-18	121	7-Day Workweek-1						-	- - 			:	RE	NSTATE	WCR3 EX	ķп				
A2750	WCR3 FENCING	23	23	09-Nov-18*	01-Dec-18	75	7-Day Workweek-1				1		1	1				1	1				1		WCF

<ul> <li>Milestone</li> <li>Critical Milestones</li> <li>Current Works</li> <li>Critical Works</li> <li>Remaining Level of</li> </ul>	CHUN WO - CRGL JOINT VENTURE	CEDD CONTRACT NO. HK/2009/02 WD II - Central Wanchai Bypass at Wan Chai East (Contract 2) 3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)	Date	Revision	Checked	Approved
---	---------------------------------	---	------	----------	---------	----------

#### Page 4 of 4

Key Dates an Sections of W KD10840 KD10860 KD10880 KD11010 KD11020	Activity Norme Revised Works Programme Rev.12.0(DD 20 N d Milestone Dates orks Completion (Included Not Granted EOT Ent Completion of Section IIIA Completion of Section IV Completion of Section VI Completion of Section VII Completion of Section VII Completion of Section IX Completion of Section IX Completion of Section X Completion of Section X		017)	08-Sep-18* 30-Aug-18* 26-Sep-18* 14-Sep-18*	Complete Complete 0% 0%	Jan	Feb Mar	Арг	May	25 Jun	BII lut	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	to Con
Key Dates an Sections of W KD10840 KD10860 KD10880 KD11010 KD11020	d Milestone Dates oths Completion (Included Not Granted EOT Ent Completion of Section IIIA Completion of Section IV Completion of Section VII Completion of Section VIII Completion of Section IX Completion of Section IX	titlement of 0 0 0 0 0 0 0		08-Sep-18* 30-Aug-18* 26-Sep-18* 14-Sep-18*	0%								чњ		107	Unit	Jan	160	- Mail	
Sections of W KD10840 KD10880 KD10880 KD11010 KD11020	Or his Completion (Included Not Granted EOT Ent Completion of Section IIIA Completion of Section IV Completion of Section VI Completion of Section VII Completion of Section VIII Completion of Section IX Completion of Section IX	0 0 0 0 0	The Contracto	08-Sep-18* 30-Aug-18* 26-Sep-18* 14-Sep-18*	0%															
KD10840 KD10860 KD10880 KD11010 KD11020	Completion of Section IIIA Completion of Section IV Completion of Section V Completion of Section VII Completion of Section VIII Completion of Section IX Completion of Section X	0 0 0 0 0	The Contracto	08-Sep-18* 30-Aug-18* 26-Sep-18* 14-Sep-18*	0%														110	
KD10860 KD10880 KD11010 KD11020	Complection of Section IV Completion of Section V Completion of Section VII Completion of Section VIII Completion of Section IX Completion of Section X	0 0 0 0		30-Aug-18* 26-Sep-18* 14-Sep-18*	0%															
KD10880 KD11010 KD11020	Completion of Section V. Completion of Section VII Completion of Section VIII Completion of Section IX Completion of Section X	0		26-Sep-18* 14-Sep-18*	0%			-					a.							
KD11010 KD11020	Completion of Section VII Completion of Section VIII Completion of Section IX Completion of Section X	0		14-Sep-18*			1	1												
KD11020	Completion of Section VIII Completion of Section IX Completion of Section X	0						-										-	-	-
100.00.000000	Completion of Section IX Completion of Section X	0			0%							1						1		
1001000	Completion of Section X	054		21-Sep-18*	0%														1	
KD11040		0		21-Sep-19*	0%														1	
KD11060	ons of Works Completion			21-Sep-18*	0%6															
Planned Sect		the second second																		
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%							1								
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%															-
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%								-							
KD10280	Planned Section VII Completion - Remainder Works	0										1							1	
KD10300	Planned Section VIII Completion - Landscape Softwork			14-Sep-18	0%		_						•						L	
C Waldalaw		0		21-Sep-18	0%			1												
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%															
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%														f.	
Dredging and							Ĩ					1							-	
Marine Work	Construction																			-
Zone CRIII					100															-1
Seawall Const	ruction - Zone CRIII																			
Zone CRIII Se	awali- 2nd Stage																			
Seeward 2 & 1					22013														ŧ.	1
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%	-		1												
Zone D	(type v, georexine and must)		(FLEETIN)									-								
Seawall Const	ruction - Zone D																		Ě.	
Seawall 10 &	1																			
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%	1.111														
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%															
MAR20570	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%													*)*********		
Works for Ser	tion Completion	and the second second																		
Construction					<u></u>			1											Ě.	
	Road A2, A4 & A5		the laboratory																Ê	
a for all the end of the							Ĩ													
Roadwork & C	tilities - Section 1 (L1806 - L1801)																		1	
Data Data	Current Milestone										-		÷ 1					Da	ite	Rev
Data Date: 20-Feb-18	Actual Work				Up	dated	Works	Prog	amm	e Re	v 12							20-Fel		12
	Critical Remaining Work						v.12 as					1								

Remaining Level of Effort

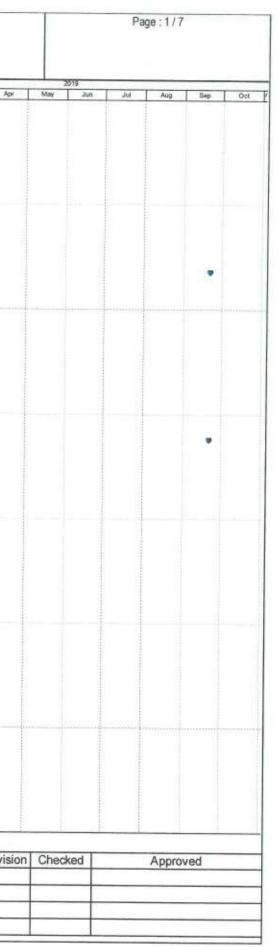

								Cent	War	h Cha	i Deve	t No. I Iopme /pass	ent Ph	10	i Wes	t							Pa	ge:2/7		
N ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	Jan F	eb Mar	Apr	May	Jun	2018 Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	2019	1			
SIIIA10279c	Sec III A - section 1 carriageway - sewerage pipe from M/H	0	02-Jan-18 A	03-Feb-18 A	100%				1.44			1.02	Sup		1454	Dar.	500	1.60	. mgi	744	may	Jun	Jul	Aug	Sep	Oct
SIIIA10293	BC to F8B (night time): construct sewerage pipe Sec III A - section 1 carriageway - sewerage pipe from M/H	6	05-Feb-18 A	26-Feb-18	0%																					
SIIIA10294	F8B - F8A (night time) Sec III A - section 1 carriageway - sewerage pipe from M/H	8	17-Jan-18 A	28-Feb-18	27.27%	-																				
SIIIA10295	F8A - F8 Sec III A - carriageway - works prrior TTA stage 5:	7	18-Jan-18 A	27-Feb-18	0%								1													
	excavation and duct laying of TCS5 and public lighting												1													
SIIIA10298	Sec III A - section 1 carriageway - works prrior TTA stage 5: road kerb	5	28-Feb-18	05-Mar-18	0%		-						1				12-2-2-1									
SIIIA10301	Sec III A - section 1 carriageway - works prrior TTA stage S: road formation	2	06-Mar-18	07-Mar-18	0%		1	-											-							
SIIIA10302	Sec III A - section 1 carriageway - works prrior TTA stage 5: laying asphalt	5	08-Mar-18	13-Mar-18	0%			-					1													
SIIIA10303	Sec III A - section 1 carriageway - works prrior TTA stage	3	14-Mar-18	16-Mar-18	0%			1																		
SIIIA10310	5: road marking & preparation works Sec III A - section 1 carriageway - TTA stage 5:	1	17-Mar-18	17-Mar-18	0%		1 R																			
SIIIA10310a	Implementation of TTA Stage 5 Sec III A - section 1 carriageway - TTA stage 5: remaining	12	19-Mar-18	04-Apr-18	0%		-	-													1000					
SIIIA10310b	sewerage pipe for M/H F8A - M/H F8 Sec III A - section 1 carriageway - TTA stage 5: remaining	18	06-Apr-18	26-Apr-18	0%			-					1							4		4			Munica	
	sewerage pipe for M/H F8A - M/H F8B	10	2012/02/02/02/02	Second Belleric																	3					
	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road- remove sheetpile at U-trough west	5	19-Mar-18	23-Mar-18	0%		-						1							1						
5IIIA10310d	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road -remove temp. road access bay 5 of SR1	21	24-Mar-18	21-Apr-18	0%		-						1													
SIIIA10310e	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road -construct upstand wall above Dwall	25	23-Apr-18	23-May-18	0%				-																	
SIIIA10310f	Sec III A - section 1 carriageway - TTA stage 5: SR1	14	24-May-18	08-Jun-18	0%					-																
SIIIA10310g	at-grade road - roadside barrier Sec III A - section 1 carriageway - TTA stage 5: SR1	7	09-Jun-18	16-Jun-18	0%			-	-	-										-	-					
SIIIA10310h	at-grade road - road formation Sec III A - section 1 carriageway - TTA stage 5: SR1	14	19-Jun-18	05-Jul-18	0%		1																			
SIIIA10312	at-grade road - laying asphalt with transition slab Sec III A - roadwork and utilities section 1 carriageway -	15	19-Mar-18	09-Apr-18	0%								-							1	1					
SIIIA10312a	Drainage works (L2202 - L2201) Sec III A - roadwork and utilities section 1 carriageway -				0%			-																		
	Drainage works (L1805 - L1801)	15	10-Apr-18	26-Apr-18	2.33		1	-																		
SIIIA10312b	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805-1807)	12	27-Apr-18	11-May-18	0%			1	-																	
SIIIA10313	Sec III A - roadwork and utilities section 1 carriageway - guly pipe (L1807 - L1801)	14	07-May-18	23-May-18	0%								-				1-1-1-1-1-1-1			1				1 + + + + + + + + + + + + + + + + + + +		
SIIIA10320	Sec III A - roadwork and utilities section 1 carriageway - fresh watermain	7	24-May-18	31-May-18	0%					-										1	1					
SIIIA10340	Sec III A - roadwork and utilities section 1 carriageway -	14	01-Jun-18	16-Jun-18	0%					1000										1						
SIIIA10360	utilities: HEC (90m) along carriageway Sec III A - roadwork and utilities section 1 carriageway -	14	19-Jun-18	05-Jul-18	0%			1												1						
SIIIA10400	road kerb & formation Sec III A - roadwork and utilities section 1 carriageway -	7	06-Jul-18	13-Jul-18	0%				8		-		i.													
SIIIA10420	black top Sec III A - Implementation of TTA Stage 7P (Closure of	1	14-Jul-18	14-Jul-18	0%	-		ļ	1		1									-	1					
	U-turn at Expo Drive)				20				1		1															
SIIIA10440	Sec III A - roadwork and utilities section 1 carriageway : breaking existing asphalt	10	16-Jul-18	26-Jul-18	0%						-									1						
SIIIA10460	Sec III A - roadwork and utilities section 1 carriageway: road kerb and formation	14	27-Jul-18	11-Aug-18	0%						1						1100			1	1					
SIIIA10480	Sec III A - roadwork and utilities section 1 carriageway : black top	10	13-Aug-18	23-Aug-18	0%				-											1						
SIIIA10500	Sec III A - roadwork and utilities section 1 carriageway : roadmarking and road furniture	14	24-Aug-18	08-Sep-18	0%				1												1					
Roadwork &	Utilities - Section 2 (L1810 - L1807)							1	1		1	E	1	1						1	ŧ	-		1111 m		199994
SIIIA12590	Sec III A - roadwork and utilities section 2 carriageway -	0	20-Jan-18 A	27-Jan-18 A	100%	-		0					8													
Roadwork &	black top Utilities - Section 3 (L1808 - L1102)								1																	
SIIIA12770	Sec III A - roadwork and utilities section 3 carriageway -	0	20-Jan-18 A	07-Feb-18 A	100%			1					1							1000						
	utilities: HEC ducting (60m) & crossroad duct (PCCW & HGC)							1	-											1	11111					
SIIIA12790	Sec III A - roadwork and utilities section 3 carriageway - road kerb & formation	17	08-Feb-18 A	10-Mar-18	0%			1	3		1									1	1					
SIIIA12810	Sec III A - roadwork and utilities section 3 carriageway - black top	7	12-Mar-18	19-Mar-18	0%		-													-		-				
Roadwork &	Utilities - Section 6 (L1102 - L1411)							1	-																	
SIIIA13399	Sec III A - roadwork and utilities section 6 carriageway -	0	12-Jan-18 A	26-Jan-18 A	100%	-		11001																		
SIIIA13444	gully pipe (L1101 -L1102) Sec III A - roadwork and utities section 6 carriageway -	0	27-Jan-18 A	03-Feb-18 A	100%	-		10000												11.0						
SIIIA13445	watermain (road crossing) Sec III A - roadwork and utilities section 6 carriageway -	13	05-Feb-18 A	06-Mar-18	0%		1														1					
	ublities: crossed duct(HEC , HGC, PCCW)	575			-			1	3		-	1	1	1						\$	1					


									Cent		D Cor Chai an Ch	Devel	opme	nt Ph	ase II		st							Page	:3/7		
γ1D.	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	Jan	Feb	Mar	Apr	May	2 Jun	Jul	Aug	Sep	Oct	Nov	Dec	line	L Ros L	10.0	1 10	2015					
SIIIA13450	Sec III A - roadwork and utilities section 6 carriageway - road kerb & formation	18	07-Mar-18	27-Mar-18	0%				3				ring	oup		- Theat	0.00	Jan	Peb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
SIIIA13470	Sec III A - roadwork and utilities section 6 carriageway -	7	28-Mar-18	09-Apr-18	0%			1	-																		
SIIIA13570	black top Achievement of Section IIIA of the Works	0		08-Sep-18	0%									ø													
Section V - Re	emaining At-Grade Road & Road P2		-																								
Roadwork &	Utilities																										
Section 1 (L1	504 - L1900)				_					-																	
SV12456	Sec V-Roadwork & Utilities Section 1 - implementation of	0	20-Feb-18*	20-Feb-18	0%			1	1	1																	
SV12460	TTA stage SE (closure of slow lane at northbound of Expo Sec V - Roadwork & Utilities Section 1 - drinage works	15	20-Feb-18	08-Mar-18	0%			1	1																		
	(L1902 - L1900)				1000														1								
SV12462	Sec V - Roadwork & Utilities Section 1 - gully pipe (L1902 - L1900)	6	09-Mar-18	15-Mar-18	0%			-																			
SV12464	Sec V - Roadwork & Utilities Section 1 - temp. reinstatement to match with existing Expo Drive	14	16-Mar-18	04-Apr-18	0%																						
SV12466	Sec V - Section 1 - Modification to 2nd stage ITA (V.O. 50) : closure of northbound and maintain one lane at southbound	1	14-Jul-18	14-Jul-18	0%							'												1			
SV12468	Sec V - Roadwork & Utilities Section 1 Carriageway - breaking existing asphalt	7	16-Jul-18	23-Jul-18	0%			ł	1			-															
5V12490	Sec V - Roadwork & Utilities Section 1 Carriageway - Road kerb & formation	10	24-Jul-18	03-Aug-18	0%							-							1								
5V12520	Sec V - Roadwork & Utilities Section 1 Carriageway - Black top	7	04-Aug-18	11-Aug-18	0%				1				-														
SV12522	Sec V - Section 1 - Implementation of TTA for road closure	3	13-Aug-18	15-Aug-18	0%			Î					8											NO.			
SV12524	of northbound and southbound of Expo Drive Sec V - Section 1 - Northbound & Southbound of Expo Drive :	14	16-Aug-18	31-Aug-18	0%				-																		
SV12526	breaking asphalt Sec V - Section 1 - Northbound & Southbound of Expo Drive :	14	01-Sep-18	17-Sep-18	0%																						
SV12528	road kerb & formation Sec V - Section 1 - Northbound & Southbound of Expo Drive :	7	18-Sep-18	26-Sep-18	0%			1						-									100				
SV12570	black top Sec V - Roadwork & Utilities Section 1 footpath -	12	29-Dec-17 A	05-Mar-18	60%			-															-				
SV12580	utilities:TCSS Sec V - Roadwork & Utilities Section 1 footpath - paving	29	06-Mar-18	12-Apr-18	0%			-	-																		
	block 1510 - L1504)		001101.10	AL 194 10					1														_				
SV12624	Sec V - Roadwork & Utilities Section 1 Carriageway - road kerb & formation	0	04-Jan-18 A	30-Jan-18 A	100%																						
SV12626	Sec V - Roadwork & Utilities Section 1 Carriageway - black top	13	31-Jan-18 A	06-Mar-18	0%					-																	
SV12692	Sec V - Roadwork & Utilities Section 2 footpath - U channel	11	17-Jan-18 A	03-Mar-18	21.43%	-		•	-																		
SV12695	Sec V - Roadwork & Utilities Section 2 footpath - Watermain	13	05-Mar-18	19-Mar-18	0%			-																			
SV12700	Sec V - Roadwork & Utilities Section 2 footpath - utilities: TCSS	16	20-Mar-18	11-Apr-18	0%			-	-																		
SV12740	Sec V - Roadwork & Utilities Section 2 footpath - paving block	18	12-Apr-18	03-May-18	0%				-	•																	
Section 3 ( C	ulvert L - L1510)							1																100			
SIV12860	Sec V - Roadwork & Utilities Section 3 footpath - Utilities:	30	16-Jan-18 A	26-Mar-18	11.76%	-		-	i l															-			
SIV12880	TCSS, HGC, PCCW) Sec V - Roadwork & Utilities Section 3 footpath - Paving	21	27-Mar-18	24-Apr-18	0%				$\rightarrow$																		
Section 4 (K)	block L106 - Culvert L)				100			1																			man
SIV12282	Sec V - Roadwork & Utilities Section 4 Carriageway -	10	20-Feb-18	02-Mar-18	0%			-																			
SIV12300	Drainage Works (L1311 - Culvert L, L1201 - Culvert L) Sec V - Roadwork & Utilities Section 4 Carriageway - Gully	7	03-Mar-18	10-Mar-18	0%			-															1	1000			
STV12302	pipe (L1301 - Culvert L, L1201 - Culvert L) Sec V - Roadwork & Utilities Section 4 Carriageway -	6			10.82873			_																			
	watermain	0	12-Mar-18	17-Mar-18	0%			1.00																			
STV12305	Sec V - Roadwork & Utilities Section 4 Carriageway - utilities : cross road duct		19-Mar-18	26-Mar-18	0%			-	-																		
SIV12310	Sec V - Roadwork & Utilities Section 4 Carriageway - Road kerb & formation : between culvert K and culvert L	15	27-Mar-18	17-Apr-18	0%																						
SIV12320	Sec V - Roadwork & Utilities Section 4 Carriageway - Black top : between culvert K and culvert L	10	18-Apr-18	28-Apr-18	0%				-	E.														-			
SIV12340	Sec V - Roadwork & Utilities Section 4 Carriageway - Black top : at west of culvert K	7	20-Feb-18	27-Feb-18	0%			E	1																		
SIV12422	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : TCSS	20	20-Feb-18	14-Mar-18	0%		F																				
SIV12440	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : HGC & PCCW	8	15-Mar-18	23-Mar-18	0%																						

								с		Wan	D Cor Chai I an Ch	Develo	opmei	nt Ph	ase II		st							Pa	ge : 4 / 7		
N ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	Jan	Feb	Mar	Apr	May		BHC Iul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	2019 Jun	UL.	Aug. 1	Sep	0 oct
SIV12460	Sec V - Roadwork & Utilities Section 4 footpath - Paving	22	24-Mar-18	23-Apr-18	0%		- 45	Contraction of the second		may	2141	24	ny	Seb	U.L.	Hur	040	0.000	res	TAL BU	1 044	anay	240	-70	Aug	sep	001
SV10300	block Achievement of Section V of the Works	0		26-Sep-18	0%																						
Section IV - S	lin Road 3							1																			
Roadwork &								1																			
Section 1 (L1	6608 - L1601)					1																					
SIV11747	Sec IV - sign gantry DS20 & DS21 footing (type 2): excavation & ELS	4	30-Dec-17 A	23-Feb-18	80.95%				1										1	5							
SIV11748	Sec IV - sign gantry DS20 & DS21 footing (type 2): footing	21	24-Feb-18	20-Mar-18	0%																1	1					
SIV11749	structure Sec IV - sign gantry DS20 & DS21 footing (type 2): removal	10	21-Mar-18	04-Apr-18	0%			-	6 I																		
SIV11751	of ELS and backfilling Sec IV - sign gantry DS21 footing (type 3): excavation	5	26-Mar-18	03-Apr-18	0%			-	1												1						
SIV11752	Sec IV - sign gantry DS21 footing (type 3): footing structure	13	04-Apr-18	19-Apr-18	0%			1 1	-												1	1					
			2024/09/10/2025	00-00000000	111000			Į					-		į						Į				*****		
SIV11753	Sec IV - sign gantry DS20: install steel frame of gantry D20	14	15-Aug-18	30-Aug-18	0%																	1					
STV11760	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L1607 - L1601)	0	09-Dec-17 A	26-Jan-18 A	100%																1	-					
SIV11761	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L1602 - L2005)	0	20-Jan-18 A	27-Jan-18 A	100%	-		1													1						
STV11762	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway -	17	29-Jan-18 A	10-Mar-18	0%			-													1						
STV11763	Drainage Works (L2103-L2101A) Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway -	21	20-Apr-18	15-May-18	0%				-												1						
SIV11764	Drainage Works (L2004 - L2005, L2101 - L2101A) Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway -	21	12-Mar-18	09-Apr-18	0%	-		-										-									
SIV11765	Gully pipe (L1607-L1601) Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway -	7	17-May-18	25-May-18	0%					1000																	
	Gully pipe (L2004)		59599991535								_										1						
SIV11780	Sec TV - Roadwork & Utilities at SR3 Section 1 Carriageway - Watermain	18	26-May-18	15-Jun-18	0%			-		100																	
SIV11800	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Utilities : TCSS crossroad duct	14	16-Jun-18	04-Jul-18	0%						8																
STV11830	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Road kerb & formation	24	05-Jul-18	01-Aug-18	0%							-									i.						
STV11840	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway -	11	02-Aug-18	14-Aug-18	0%								-														
SIV11860	Black top Sec TV - Roadwork & Utilities at SR3 Section 1 footpath -	7	26-May-18	02-Jun-18	0%		1011		1												1						
SIV11880	Drainage Works: future connection pipes Sec IV - Roadwork & Utilities at SR3 Section 1 footpath -	7	04-Jun-18	11-Jun-18	0%						-																
SIV11900	watermain Sec IV - Roadwork & Utilities at SR3 Section 1 footpath -	39	12-Jun-18	28-Jul-18	0%						_																
	utilities: HEC & TCSS												_									1					
SIV11920	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - paving block	17	30-Jul-18	17-Aug-18	0%				1			3.									i .	Ĵ.					
Section 2 ( L	2301 - L2103)																										
SIV11942	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Gully pipe (L2301-L2013, L1608-L1609)	0	28-Dec-17 A	23-Jan-18 A	100%																						
SIV11960	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway -	0	24-Jan-18 A	03-Feb-18 A	100%			_													1	-					
SIV12010	Watermain Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway -	20	05-Feb-18 A	14-Mar-18	0%		-														1						
SIV12020	Road kerb & formation Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway -	7	15-Mar-18	22-Mar-18	0%																1						
SIV12040	Black top Sec. IV - Roadwork & Utilities at SR3 Section 2 footpath -	7	07-Mar-18	14-Mar-18	0%			-				-31000 pr	8000 Marine								<u> </u>	÷					
	Drainage Works: future connection pipes								_ 1																		
SIV12060	Sec TV - Roadwork & Utilities at SR3 Section 2 footpath - utilities: TCSS	25	15-Mar-18	17-Apr-18	0%															8		1					
STV12080	Sec IV - Roadwork & Utilities at SR3 Section 2 footpath - paving block	21	18-Apr-18	12-May-18	0%			1													1	1					
Section 3 ( )	4/H1.6 - L2301)							1													1						
STV12092	Sec TV - Roadwork & Utilities at SR3 Section 3 Carriageway -	38	28-Dec-17 A	09-Apr-18	35.59%	-		-	•												1						
SIV12096	Drainage Works (M/H1.7 - L2301) Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway	0	29-Nov-17 A	24-Jan-18 A	100%	-						Cr=1	·····		<u></u>	Sectors 10		00315221				÷	+++++++++++++++++++++++++++++++++++++++	······			100400
SIV12102	M1.7-ML.6: construct manholes Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	0	25-Jan-18 A	08-Feb-18 A	100%			1	1																		
	M1.7-M1.6: demolish existing seawall Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	10		02-Mar-18	0%6																1						
SIV12103	M1.7-M1.6: ELS		09-Feb-18 A				T		_												1						
SIV12104	Sec TV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: Construct manhole & pipes	30	03-Mar-18	11-Apr-18	0%			1																			
SIV12120	Sec TV - Roadwork & Utilities at SR3 Section 3 Carriageway Drainage Works (M1.6-C1.1-C1.2): ELS,construct MH and	28	12-Apr-18	15-May-18	0%			1	-										1		1						

					1-11-0-0-0-0-0-0-0-0-0-0-0-0-0-0-0-0-0-			Cer		D Cor Chai I an Ch	Develo	opme	nt Pha	ase II		st							Pa	ge : 5 / 7		
avity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	Jan	Feb	the L		20	518						-		in the second		-	2019	15 1165			
SIV12121	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	6	16-May-18	23-May-18	0%	Jan	Peo	Mar Aş	e May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Dct
SIV12122	Drainage Works (M1.6-C1.1-C1.2): Backfilling & shift lane Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	5	24-May-18	29-May-18	0%														1	1						
	Drainage Works (M1.6-C1.1-C1.2): Construct MH C1.2	-	STATISTICS.		2013																					
SIV12140	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Gully pipe (M/H 1.7 - L2301)	32	10-Apr-18	17-May-18	0%																					
STV12150	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Road kerb	14	18-May-18	04-Jun-18	0%												0	Č.								
SIV12155	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	10	05-Jun-18	15-Jun-18	0%					-																
STV12160	formation Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	7	16-Jun-18	25-Jun-18	0%					-							-	-								
	Black top				6.12					_																
SIV12170	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Utilities: TCSS	21	10-May-18	04-Jun-18	0%																					
SIV12180	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - U channel	10	05-Jun-18	15-Jun-18	0%					-																
SIV12220	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath -	25	16-Jun-18	17-Jul-18	0%					-											1					
STV12222	Paving block Achievement of Section IV of the Works	0		30-Aug-18	0%																					
				So may to					E.																	
Section VII -	Remainder Works																			1		I.				
Road & Drain	nage Works (Culvert L - M/H1.7, Adjacent to SR3)					1	1											100	-							
SVII11600	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	48	08-Jan-18 A	20-Apr-18	18.64%	-		-	3																	
SVII11620	Drainage Works (Culvert L -MH1.7) Sec TV - Roadwork & Utilities at SR3 Section 4 Carriageway :	3	21-Apr-18	24-Apr-18	0%														1							
	traffic diversion at Lung King Street		- constance	- and - march	151.0				-																	
SVII11640	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Gully pipe (Culvert L -MH1.7)	27	25-Apr-18	28-May-18	0%													1	1	-	1					
SVII11650	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - TCSS duct	7	29-May-18	05-Jun-18	0%		1			-							-									
SVII11654	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	14	06-Jun-18	22-Jun-18	0%					-									1							
SVII11660	road kerb & formation Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	6	23-Jun-18	29-Jun-18	0%														1	1						
	Black top				51651		1																8			
SVII11680	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - U channel	14	29-May-18	13-Jun-18	0%			-		-											-					
SVII11700	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - utilities: TCSS	14	14-Jun-18	30-Jun-18	0%																					
SVII11720	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath -	14	03-Jul-18	18-Jul-18	0%		1			1										-	-					
Retaining Wa	paving block all RW5 Construction					1 1														10 III	Î.					
			20.11.10																-							
SVII10660	Sec VII - Retaining Wall RW5 (bay 1) - construct base slab and wall	22	20-Mar-18	18-Apr-18	0%														1	1	-					
SVII10680	Sec VII - Retaining wall RW5 (bay 2) - construct base slab and wall	22	19-Apr-18	15-May-18	0%																1					
SVII10800	Sec VII - Retaining wall RWS (bay 3) - construct base slab	22	20-Mar-18	18-Apr-18	0%														1							
SVII10820	and wall Sec VII - Retaining wall RW5 (bay 4) - construct base slab	22	19-Apr-18	15-May-18	0%																					
SVII10860	and wall Sec VII - Retaining wall RW5 - curing, removal formwork			101000000 C C C C C C C C C C C C C C C					-			1														
	President and an and a second president and a second second second second second second second second second s	0	16-May-18	25-May-18	0%		1		-									1								
Landing Step	s Construction						1					1											1			
Landing Step	os BSW13																					1 1				
SVII10900	Sec VII - Landing steps (8SW13) - install vertical fender /	15	15-May-18	01-Jun-18	0%		1																			
SVII10920	step fender Sec VII - Landing steps (BSW13) - install s.s. handrail /																	1	1							
	tactile / sign board / boilard	25	02-Jun-18	03-Jul-18	0%			1																		
Landing Step	35 B5W4																									
SVII10980	Sec VII - Landing steps (BSW4) - install vertical fender / step	15	20-Jun-18	07-Jul-18	0%		ŧ			E.c.																
SVII11000	fender Sec VII - Landing steps (BSW4) - Install s.s. handrail / tactile	25	09-Jul-18	06-Aug-18	0%						-															
Landing Step	/ sign board / bollard	1977	\$050750773	25701011.25	202																					
SVII11060	Sec VII - Landing steps (8SW5) - install vertical fender / step fender	15	25-Jul-18	10-Aug-18	0%						-						11111111	-								
SVII11080	Sec VII - Landing steps (BSW5) - install s.s. handrail / tactile	25	11-Aug-18	08-Sep-18	0%							-	-													
Landing Step	/ sign board / bollard as BSW9											-														
SVII11140		10	12.1	20 1						_		1											11111			
	Sec VII - Landing steps (BSW9) - install vertical fender / step	15	13-Jun-18	30-Jun-18	0%	1 3		1	1			1						8				1 3				
SVII11160	fender Sec VII - Landing steps (BSW9) - install s.s. handrail / tactile					1	1.00		3									8					- 2			

						CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central - Wan Chai Bypass at Wan Chai West	Page : 6 /	7
wiy ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018 Jain Feib Mai Apr Mey Jun Jul Aug Sep Oct Nov Dec Jan Peb Mar Apr May	2019	1
Promenade	Seawall Parapet Construction & EVA					Jan Feb Mar Apr Mey Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May	Jun Jul Aug	Sep Oct
SVII12000	Sec VII - Precast parapet	67	18-Nov-17 A	14-May-18	0%			
SVII12010	Sec VII - Zone CRIII - seawall parapet: Backfiling	14	20-Feb-18	07-Mar-18	0%			
SVII12120	Sec VII - Zone CRIII - seawall parapet: Construct mass	30	08-Mar-18	16-Apr-18	0%			
	concrete coping			****				
SVII12122	Sec VII - Zone CRIII - seawall parapet: reinforced concret coping	17	17-Apr-18	07-May-18	0%			
SVII12140	Sec VII - Zone CRIII - seawall parapet: construct seawall parapet	30	08-May-18	12-Jun-18	0%			
SVII12160	Sec VII - CRIII - EVA: watermain	14	13-Jun-18	29-Jun-18	0%			
SVII12180	Sec VII - CRIII - EVA: U-channel	14	30-Jun-18	17-Jul-18	0%			
SVII12200	Sec VII - CRIII - EVA: bituminous layer	5	18-Jul-18	23-Jul-18	0%			
SVI112220	Sec VII - CRIII - EVA: paving block	30	24-Jul-18	27-Aug-18	0%			
SVII13120	Sec VII - Zone A1, A2 & B - seawall parapet: Construct mass	14	28-Dec-17 A	07-Mar-18	68.18%			
SVII13122	concrete coping Sec VII - Zone A1, A2 & B - seawall parapet: reinforced	18	08-Mar-18	28-Mar-18	0%			
	concrete coping	30			0%			
SVII13140	Sec VII - Zone A1, A2 & B - seawall parapet: Construct seawall parapet		09-Apr-18	14-May-18				
SVII13160	Sec VII - Zone A1, A2 & B - EVA: watermain	14	15-May-18	31-May-18	0%			
SVII13180	Sec VII - Zone A1, A2 & B - EVA: U-channel	14	01-Jun-18	16-Jun-18	0%			
SVII13182	Sec VII - Zone A1, A2 & B - EVA: bituminous layer	5	19-Jun-18	23-Jun-18	0%			
SVII13184	Sec VII - Zone A1, A2 & B - EVA: paving block	30	25-Jun-18	30-Jul-18	0%			
SVII13200	Sec VII - Zone D - seawall parapet: Remove temporary	21	07-Mar-18	03-Apr-18	0%			
SVII13220	seawall block Sec VII - Zone D - seawall parapet: Construct mass concrete	30	04-Apr-18	10-May-18	0%			
SVII13222	Sec VII - Zone D - seawall parapet: reinforced concrete	18	11-May-18	01-Jun-18	0%			
SVII13240	coping Sec VII - Zone D - seawall parapet: Construct seawall	25	02-Jun-18	03-Jul-18	0%			
	parapet							
SVII13260	Sec VII - Zone D - EVA : watermain	14	04-Jul-18	19-Jul-18	0%			
SVII13280	Sec VII - Zone D - EVA : U-channnel	14	20-Jul-18	04-Aug-18	0%			
SVII13300	Sec VII - Zone D - EVA : bituminous layer	5	05-Aug-18	10-Aug-18	0%			
SVII13320	Sec VII - Zone D - EVA : paving block	30	11-Aug-18	14-Sep-18	0%			
Promenade	Footpath							
Settion 1					State Ha			
SVII10440	Sec VII - section 1 footpath - drainage works : connection	10	24-May-18	04-Jun-18	0%			
Constant of	pipe & U -channel Sec VII - section 1 footpath - watermain	7	05-Jun-18	12-Jun-18	0%			
		7	13-Jun-18	21-Jun-18	0%			
1000 E. 10100 (1000)	Sec VII - section 1 footpath - lighting							
	Sec VII - section 1 footpath - paving block	21	22-Jun-18	17-Jul-18	0%			
Section 2					1.2			
SVII12610	Sec VII - section 2 footpath - drainage works : L2202 - L2203A	20	20-Feb-18	14-Mar-18	0%			
SVII12615	Sec VII - section 2 footpath - watermain	7	15-Mar-18	22-Mar-18	0%			
SVII12630	Sec VII - section 2 footpath - utilities: TCSS	21	23-Mar-18	20-Apr-18	0%			
SVII12670	Sec VII - section 2 footpath - paving block	30	21-Apr-18	28-May-18	0%			
Section 3								
	Sec VII - section 3 footpath - watermain	17	20-Feb-18	10-Mar-18	0%			
See 2 of A Content	e senserer, with the test test test test test							
SVII12870	PCCW)	40	12-Mar-18	02-May-18	0%			
SVII12875	Sec VII - 3 footpath - drainage works :U chanel	14	03-May-18	18-May-18	0%			

		-							Centr	Wan	Chai	ntract Devel hai By	opme	nt Ph	ase II		t				
y ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	Jan	Feb	Mar	1 4.4	1 11-1		2018	1 4 4	1	1	1 10					-
SVII12890	Sec VII - section 3 footpath - paving block	30	19-May-18	25-Jun-18	0%	Jan	Feb	Mar	Apr	May	Jun	bL	Aug	Sep	Oct	Nov	Dec	net	Feb	Mar	Apr
					5.1.5																100
SVII13049	Sec VII - section 4 footpath - watermain	1	14-Nov-17 A	20-Feb-18	95.24%	-	-														
5VII13050	Sec VII - section 4 footpath - drainage works (L2203	21	21-Feb-18	16-Mar-18	0%		and a second														
SVII13055	-L2203A) Sec VII - section 4 footpath - utilities: HEC, TCSS, HEC &	49	17-Mar-18	18-May-18	0%			C==						1							
SVII13110	PCCW Sec VII - section 4 footpath - paving block	25	19-May-18	19-Jun-18	0%					-	-										-
Section 57					1000																
SVII13270		14	17-Mar-18	06-Apr-18	0%			-	-												
SVII13275	-L2204 Sec VII - section 5 footpath - watermain	14	07-Apr-18	23-Apr-18	0%																1
SVII13310	Sec VII - section 5 footpath - utilities: HEC, TCSS, HGC,	42	24-Apr-18	13-Jun-18	0%						-										
SVII13330	PCCW Sec VII - section 5 footpath - paving block	22	14-Jun-18	11-Jul-18	0%			-			-	-			84444						1
Section 9					172175			1													1111
SVII13490	Sec VII - section 6 foolpath - drainage works(Culvert L -	14	20-Feb-18	07-Mar-18	0%			Tenina	-												
SVII13510	L2204) Sec VII - section 6 footpath - watermain	13	08-Mar-18	22-Mar-18	0%																
SVII13514	Sec VII - section 6 footpath - U channel	20	23-Mar-18	19-Apr-18	0%				-												
SVII13530	Sec VII - section 6 footpath - utilities: HEC, TCSS, HGC,	49	23-Mar-18	25-May-18	0%					-											
SVII13550	PCCW Sec III A - section 6 footpath - paving block	25	26-May-18	25-Jun-18	0%																
SVII19420		0		14-Sep-18	0%																
Section VIII -	Landscape Softworks				and the second																
Soft Landsca																					
SVIII10040	Sec VIII - Trees Planting	141	04-May-18	21-Sep-18	0%	-	-			0		Kanadali		-							-
SVIII10060	Sec VIII - Shrubs Planting	141	04-May-18	21-Sep-18	0%						-										
SVIII 10080	Achievement of Section VIII of the Works	0	0.1100 20	21-Sep-18	0%																
ulos sources.c.	Stablishment Works	1.00		#1 30p 13	0.10																
Soft Landsca					Correct of the																
SEX10020	Sec IX - Establishment Works	365	22-Sep-18	21-Sep-19	0%	-	1	1	1												1
SEX10020	Achievement of Section IX of the Works	0	xx-3ch-10	21-Sep-19	0%																1
Treesenation,	rotection & Preservation of Trees	v		21-36p-19	0.30																0.000
					14.2																1
ALCONGES.	Section X - Protection & Preservation of Trees													1							1
SX10000	Achievement of Section X of the Works	0		21-Sep-18	0%		1					-									1
Soft Landsca																					1
SX10020	Sec X - Protection & Preservation of Trees	214	31-Jan-13 A	21-Sep-18	86.89%																

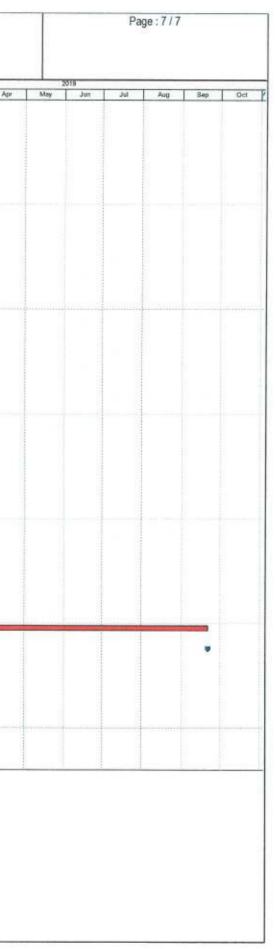

tivity ID	Activity Name	Rem	Start	Finish	Decembe	2018 Vr			lor	any			Echri	201 2rv
		Dur				er 6	23	30	Janu 06 13		27	03	Febru 10	
3MRP (2018.	.12.20)													
10 - SECTION	N X OF THE WORKS													
10.3 - Middle	Bridge (Bridge F)											1 1 1 1		
10.3.2 - Bridg	e Construction													
Outstanding	g Works			-										
1032-4430	Install remaining standard traffic & directional sign (NW)	28	26-Dec-18	28-Jan-19			▶	;			In:	stall remain	ing stand	ard
1032-4440	Removal of Temporary JTI sign gantry at Tong Sui Slip Road (NW)	28	29-Jan-19	05-Mar-19	-			     				1 1 1		
1032-4480	Concrete Surround for TCSS Ducting at Existing IEC bridge 8 bays (NW)	25	05-Nov-18 A	19-Jan-19				 		Conc	rete Surro	und for TC	SS Ducti	ıg
1032-4520	Maintenance walkway & Fall Arrest system at Green Roof	45	26-Dec-18	20-Feb-19	-		<b>&gt;</b>	 						
1032-4530	Remedial Works to Marine Pile Caps	21	26-Dec-18	19-Jan-19	-		►			Reme	edial Wor	ks to Marine	e Pile Ca	s
10.6 - Tunnel	Approach Ramp													
10.6.1 - Appro	oach Ramp (Excluding Portion IIB)							     				1 1 1 1		
Landscape [	Deck							     				1 1 1 1		
1061-7479	Bay C1-C5 > Type 2 Railing Above Landscape Deck (East & West side)	15	06-Oct-18 A	08-Jan-19	_				Bay C1-C	25 > Type 2	Railing A	bove Lands	cape De	:k (
1061-7520	Bay C1 > Sub-soil placing	25	20-Dec-18	19-Jan-19	-				-		-	soil placing		
1061-7540	Bay C2 > Screeding/Drainage Layer/Root Barriers	25	20-Dec-18	19-Jan-19						[		eding/Drain		 /F
1061-7560	Bay C2 > Sub-soil placing	25	21-Jan-19	21-Feb-19	-							- <b>3</b>		
1061-7580	Bay C3 > Screeding/Drainage Layer/Root Barriers	26	21-Jan-19	22-Feb-19	-			     						_
1061-7700	Bay C3 > Sub-soil placing	21	23-Feb-19	19-Mar-19	-			     				1 1 1		
	n X - Miscellaneous Works		2010010					     						
10.7.1 - TTM S								       				     		
1071-1760	TTM Stage 10 - Tunnel Commisioning	0	1	24-Dec-18*	-				innel Comn	icionina				
		0		24-Dec-10		Ĭ		aye 10 - 11		iisioiiiig				
10.7.3 - Open														
	apet and Hard Paving Works Along Sea Wall				-				0	0.1				
1073-1000	Design and Submission Confirmation, Site Clerance and cut the rebar	0		20-Dec-18*	F		sign and S	Submission	Confirmatio	on , Site Cie	erance an	d cut the ret	)ar	
1073-1040	Order and Casting of Precast Block 453 nos x 1.5m long (680m) , 1st 90 nos 1 month production, 12 day per 90 nos	79	20-Dec-18	08-Mar-19				- - - - -				1		
1073-1080	Drill holes for anchor at sea side block 453 nos, 10 nos per day	38	20-Dec-18	04-Feb-19	4			   				Drill	holes for	a
Masking Wa	ll to D12		,											
1073-1500	South Part	7	02-Jan-19	09-Jan-19			1		South P	art		-       		
1073-1540	Middle Part	8	10-Jan-19	18-Jan-19	-			l	►	Middle	Part			
1073-1580	North Part	7	19-Jan-19	26-Jan-19						▶	North	Part		
	tanding Drainage Works	J.	<u></u>									1 1 1 1		
10.7.4 - Outst						1						1 1 1		
	2 to Pier D7 from Pier D9-D12							1				1		
		12	15-Dec-18 A	04-Jan-19				300	)pipe with c	oncrete sur	round > 1	- 62 to CP-	62A (19.5	m
Near Pier D1	2 to Pier D7 from Pier D9-D12	12 9	15-Dec-18 A 05-Jan-19	04-Jan-19 15-Jan-19	-	_		300 				- 62 to CP- te surround		,

		Re

Actual Work

emaining Level of Effort Remaining Work

Actual Level of Effort

Critical Remaining WorkMilestone

### Contract HY/2009/19 Three Months Rolling Programme (20.Dec.2018 to 20.Mar.2019)

19							
17	24	03	2	March	17	24	April 31 /
17	24		,		17	24	<u> </u>
							1
							1
							1 
							1
							1 1 1
traffic	& direct	ional sig	n (NW	V)			
			Remo	oval of Tem	iporary	JTI sign ga	antry at Tc
t Existi	ng IEC	bridge 8	bays	(NW)			1
<b>—</b> M	aintena	nce wall	wav &	& Fall Arres	st svste	m at Green	Roof
			,		,		 
							1
							1 1
East &	West si	de)					1
							1 1 1
oot Bar	riers						
	Bay C2	> Sub-so	oil pla	cing			1
	Bay C		dina/	Drainage I	aver/F	loot Barrier	ý 2
	Day OC	/ / 00/00	sung/	Diamager			1
					Bay	/ C3 > Sub-	soil placir
							1
							, , ,
							1
							1
							1 1 1
							1
							1
			<b>—</b> C	order and C	asting	of Precast	Block 453
chor at	sea sid	e block 4	153 no	os, 10 nos p	ber day	/	1
							1 1 1
							r ! !
	vert (7m	)					1
P-D111	to 1-61A	A (8m +	9m)				
					Dago	1 of 4	
					rage	1014	

Activity ID	Activity Name	Rem Dur	Start	Finish	2018 December	2019 January February
1070 0000			04 Jan 10	11 Eak 10	16 23	30 06 13 20 27 03 10 17 24 03
1073-2360	450pipe > 1-67 to 1 -68 (30.5m)	13	24-Jan-19	11-Feb-19	_	450pipe > 1-67 to 1 -68 (30.5m)
1073-2400	450pipe > 1-68 to Box Culvert @ +0.88mPD (8m)	8	12-Feb-19	20-Feb-19		450pipe > 1-68 to Box Ci
Bet Pier D19	-D26 - West of SR13 to Box Culvert (to commence after removal of girder)					
1073-2760	225 U Channel (4days/20m) (110m)	24	02-Jan-19*	29-Jan-19		225 U Channel (4days/20m) (110m)
1073-2800	Drain pit to Sand Trap with 225 pipe (10m)	5	30-Jan-19	04-Feb-19		Drain pit to Sand Trap with 225 pipe (10m)
1073-2840	Sand Trap to Box ,225 pipe (6m)	6	08-Feb-19	14-Feb-19	_	Sand Trap to Box ,225 pipe (6m)
Bet Pier P20-	-P26 - Under Westbound Bridge (to commence after removal of site office)					
1073-2880	225 U Channel at site office and West bound SR13(4days/20m) (124m)	34	30-Jan-19*	13-Mar-19		
1073-2920	225 pipe > Pier 22 Catch Pit to Ex. MH (15m)	5	30-Jan-19	04-Feb-19	-	225 pipe > Pier 22 Catch Pit to Ex. MH (15m)
1073-2960	300pipe > 1-40C to Ex. MH, 1-40C to 225U Channel (21+6.5m)	10	08-Feb-19	19-Feb-19		→ 300pipe > 1-40C to Ex. MI
Bet Pier P28-	-P35 - ADB area (to commence after LJV works - 1/12/2019)					
1073-3200	150 U Channel at ADB (83m)	20	03-Jan-19*	25-Jan-19		150 U Channel at ADB (83m)
1073-3240	Paving Block at ADB (140m2)	9	26-Jan-19	08-Feb-19	-	Paving Block at ADB (140m2)
1073-3280	225 pipe > 1-52A to DP1-52A (13m)	8	02-Jan-19*	10-Jan-19	-	225 pipe > 1-52A to DP1-52A (13m)
1073-3320	225 U Channel, narrow condition, 6days / 20m (65m)	20	11-Jan-19	02-Feb-19		225 U Channel, narrow condition, 6days / 20m (6
1073-3360	300 pipe > 1-47D to 1-48B (19m)	7	02-Jan-19	09-Jan-19	-	300 pipe > 1-47D to 1-48B (19m)
1073-3400	375 pipe > 1-48B to 1-50 and 1-50 to 1-51 (10+5m)	7	11-Jan-19	18-Jan-19	-	375 pipe > 1-48B to 1-50 and 1-50 to 1-51 (10+5m)
1073-3440	2 Catch pit to 1-47D (5+6m)	5	10-Jan-19	15-Jan-19	-	► 2 Catch pit to 1-47D: (5+6m)
1073-3480	300 UC 6days/20m (103m)	32	09-Feb-19	18-Mar-19	-	
11 - SECTION	I 11 OF THE WORKS					
11.4- Hing Fat						
Time for Trial	Run & RC preparation period					
1140-1010	RC Preparation Period	2	20-Nov-18 A	21-Dec-18	RC Prepar	ration Period
Tsing Fung S	treet (Left side) Kerbline underneath flyover (CWBIEL/058 - 111)					
1140-1020	Construct new kerb and relocate gully	46	22-Dec-18	19-Feb-19		Construct new kerb and re
	and at Tsing Fung Street and Hing Fat Street Junction (North side) (CWBI		00)			
1140-1040	Construct new kerb, relocate gully, dwarf wall, beam barrier, irrigration pipe	46	22-Dec-18	19-Feb-19		Construct new kerb, reloc
	(CWBIEL/058 - 111)					
	eet (S/B) Slow Lane					
1140-1260	Breaking existing pavement and excavation	6	22-Dec-18	29-Dec-18	·····	Breaking existing pavement and excavation
		6				
1140-1280	Laying underground ducting & backfilling	6	31-Dec-18	07-Jan-19		Laying underground ducting & backfilling
1140-1300	Reconstruction pavement & road marking	6	08-Jan-19	14-Jan-19		Reconstruction pavement & road marking
	itreet Footpath					
1140-1320	Breaking existing footpath and excavation	6	22-Dec-18	29-Dec-18		Breaking existing footpath and excavation
1140-1340	Laying underground ducting and backfilling	6	31-Dec-18	07-Jan-19		Laying underground ducting and backfilling
1140-1360	Reconstruction footpath	6	08-Jan-19	14-Jan-19		Reconstruction footpath
Triangular Is	land at Victoria Park Road (East side)					
Remaining	Level of Effort Remaining Work				Cont	ract HY/2009/19
Actual Leve	-		Th	ree Month		jramme (20.Dec.2018 to 20.Mar.2019)
Actual Wor	rk					

					201	19										
-			F	ebru	lary	47			00		March			04	Ap	
<u> </u>	03	3		10 450	Dining	17	2		03 8 (30.5m)	1	0	17		24	31	ľ
1				400	pipe		1-07 10 1	-0	0 (30.311)							
							450pipe	₹÷	1-68 to Box	Culv	vert @	+0.88r	nPD	(8m)		
225	J Ch	nann	iel (	4day	/s/20	)m) (	(110m)									
		)rair	n nit	to S	Sand	Tra	n with 22	25	pipe (10m)							
	<u> </u>		. թ.,													
-	4				Sar	nd Ti	rap to Bo	ж¦,	225 pipe (6	Sm)						
į											225	U Cha	nnel	at site	office	and
	2	25 p	oipe	> Pi	ier 2	2 C	atch Pit t	οE	Ex. MH (15m	ו)						
							2000			N 41 1	1 400	ta 005		boonal	(01.)	
						<b>_</b> ,	soopipe	>;ı ¦	1-40C to Ex.	w⊓,	1-400	10 223	50 0	nannei	(21+ ¦	0.5111
J Cha	nnol	lati		3 (83	m)										1	
		/														
1		2	Pa	ving	Bloc	k at	ADB (14	l0n	n2)						}	
52A (*	13m)	)														
<u></u> `		l	 \k													
	225		nar	nnei,	nar	row	conditio	n,¦e	6days / 20m	(650	n)					
(19m	)															
; 8B to	1-50	an	d 1-	50 ta	n 1-5	51 (1	l0+5m)									
				00 1	510	, (	lo rom)									
D¦(5+	6m)															
-												300	UC	6days/2	20m (	103n
															÷	
-							Construc	t n	iew kerb and	d relo	cate g	ully				
							Construc	+ -	iew kerb, rel	ocate		dwarf	wall	boam	borri	or ir
							Constitue			ocale	s guny,	uwan	wan	, beam		сı, п
n¦																
back	fillin	g														
ment	& ro	ad r	nar	kina												
	0.10	uui	nan	ang												
-																
nd ba		line														
nd ba	ICKIII	iing													}	
ath																
				( <b>^</b> )								Pag	e 2 d	of 4		
20. <b>I</b>	via	r.2	201	19)												

Activity ID		Activity Name	Rem	Start	Finish			018							2019									
			Dur			Decemb	ber 16 23		January 30 06 13 20			27	February 7 03 10 17 24				03	March 03 10 17 24			April 31			
1	140-1060	Breaking local area at island and excavation	6	22-Dec-18	29-Dec-18				Breaki	ing local	area	a at island and e	cavation	1						L	•			
1	140-1080	Laying underground ducting for traffic light and lighting pole & backfilling	6	31-Dec-18	07-Jan-19	_		L	-	La	iying	underground du	cting for	traffic lig	ht and lig	hting pole &	& backfill	ing						
1	140-1100	New kerb construction and relocate traffic light and lighting pole	6	08-Jan-19	14-Jan-19					►		New kerb cor	struction	and relo	cate traffi	c light and l	ighting	ole						
1	140-1120	Removal of existing kerb and existing lighting pole	6	15-Jan-19	21-Jan-19	_					-	Rer	noval of	existing k	erb and e	existing light	ting pole	1 1 1 1						
1	140-1140	Reconstruction pavement	8	22-Jan-19	30-Jan-19	-						▶		Reconstru	uction pay	vement		     						
Tr	iangular Isla	and at Victoria Park Road (South side)																     						
1	140-1160	Breaking existing pavement (Victoria Park Road slow lane) and excavation	10	22-Dec-18	04-Jan-19		┕	-	<u> </u>	Breaki	ng e	xisting pavemen	t (Victoria	a Park Ro	ad slow l	ane) and e	xcavatio	י ח						
1	140-1180	Laying underground ducting for traffic light and backfilling	4	05-Jan-19	09-Jan-19					-	Layi	ng underground	ducting f	for traffic	light and	backfilling		     						
1	140-1200	New kerb construction and relocate traffic light	3	10-Jan-19	12-Jan-19	_						New kerb constr	uction an	nd relocat	e traffic li	ght		,     						
1	140-1220	Removal of existing kerb and existing lighting pole	3	14-Jan-19	16-Jan-19	_						Removal c	fexisting	g kerb and	d existing	lighting pol	е	1 1 1						
1	140-1240	Remaining island construction included Beam Barriers, Type 2 Railing	20	17-Jan-19	12-Feb-19	-									F	Remaining i	sland co	nstruction	includeo	d Beam Ba	arriers, Type	2 Railing		
Sta	age 2 (CWB	IEL/058 - 094)																     						
		et (S/B) Fast Lane																   						
	140-1380	Breaking existing pavement and excavation	6	15-Jan-19	21-Jan-19						Ļ	Bre	aking exi	sting pave	ement an	d excavatio	n							
	140-1400	Realignment of road marking (3 N/B lanes), nightime	3	15-Jan-19	17-Jan-19	_					[					lanes), nig								
	140-1420	Laying underground ducting & backfilling	4	22-Jan-19	25-Jan-19	_										ing & backfi		1 1 1 1						
	140-1440	New island construction and temp traffic light	3	26-Jan-19	29-Jan-19	_										tion and te	-	e light						
	140-1460	Removal of existing island and traffic light	3	30-Jan-19	01-Feb-19											sting island		,						
	140-1480		3	02-Feb-19	01-Feb-19 08-Feb-19	_										-		1	wh+					
		EMSD's connection to temp traffic light				_										)'s connectio		1	JUL					
	140-1500	Reconstruction pavement & road marking	7	26-Jan-19	02-Feb-19							-	·		nstruction	n pavement	& road r	narking ¦						
	<u> </u>	IEL/058 - 021)																1 1 1 1						
<b>.</b>		et (N/B) Left 3 Lane																     						
	140-1520	Breaking existing pavement and excavation	7	09-Feb-19	16-Feb-19	_								4		Breaki	-	ng paveme						
1	140-1540	Laying underground ducting & backfilling	6	18-Feb-19	23-Feb-19												📕 Layir	ig undergro	ound due	cting & bad	ckfilling			
1	140-1560	Reconstruction pavement & road marking	6	25-Feb-19	02-Mar-19													Recon	structior	n pavemer	nt & road ma	ırking		
12 -	SECTION	7, 8, 9, 10 & 12 OF THE WORKS																     						
12.1	1 - Perman	ent Noise Mitigation Measures																     						
We	est Bound B	rigde Between F2 to C2 (P40 to P22) (parapet mould 1)																						
12	210-1000	TTA Stage 1 - Close 2 lane (1 & 2) for traffic from Pier 41	6	26-Dec-18*	02-Jan-19				י 🛁	FTA Stag	je 1 -	Close 2 lane (1	& 2) for	traffic fror	m Pier 41			1 1 1 1						
12	210-1040	Bridge F2C (F3-F5) - Preparation works; Remove asphalt & drill holes for starter bars	10	03-Jan-19	14-Jan-19	_						Bridge F2C (	F3-F5) -	Preparati	ion works	; Remove a	sphalt &	drill holes	for start	er bars				
12	210-1080	Bridge F2C (F3-F5) - Construction of inner parapet (52m)	14	15-Jan-19	30-Jan-19	-					-	<b>-</b>		Bridge F2	2C (F3-F	5) - Constru	iction of	inner para	pet (52m	ו)				
12	210-1120	Bridge F2C (F3-F5) - Installation of permanent post	12	31-Jan-19	16-Feb-19	_										Bridge	e F2C (F	3-F5) - Ins	tallation	of perma	nent post			
12	210-1160	Bridge F2C (F3-F5) - Removal of temporary roof beam & panel	12	18-Feb-19	02-Mar-19											•··		Bridge	e F2C (F	3-F5) - R	emoval of te	mporary		
12	210-1320	Bridge F1C (D12-F3 - Preparation works; drill holesclean couplers for starter	10	15-Jan-19	25-Jan-19	1					Ļ		Bridge	F1C (D12	2-F3 - Pr	eparation w	orks; dri	II holesclea	an coupl	ers for sta	rter bars			
12	210-1360	bars Bridge F1C (D12-F3 - Construction of inner parapet (88.4m)	21	26-Jan-19	22-Feb-19							⊨					Bridge	F1C (D12	-F3 - Co	onstruction	n of inner pa	rapet (88		
12	210-1400	Bridge F1C (D12-F3 - Installation of permanent post	18	12-Feb-19	04-Mar-19	_									╘┝┏═	_		Brid	dge F1C	(D12-F3	- Installatio	n of perm		
12	210-1560	Bridge C5 (P32-D12) - Preparation works; drill holesclean couplers for starter bars	10	26-Jan-19	09-Feb-19	-									Bridg	ge C5 (P32-	·D12) - F	reparation	works;	drill holes	clean coupl	ers for sta		
	Remaining I	Level of Effort Remaining Work	1	1	1		-	<b>^</b>			200	0/10												
	Actual Level	l of Effort Critical Remaining Work		<b></b>						: HY/2				0 N/	0040	•			Page 3 of 4					
	Actual Work	<ul> <li>♦ Milestone</li> </ul>		Ih	ree Month	IS KO	omr	ng Pro	gram	ıme (	20.	.Dec.2018	5 to 20	u.Mar	.2019	)								

ctivity ID		Activity Name		Start	Finish	2018									2019
						December			20	January 30 06 13			20 27		February 10
1210	D-1600	Bridge C5 (P32-D12) - Construction of inner parapet (77.85m)	21	13-Feb-19	08-Mar-19		<u> </u>		30	00	13	20		03	
Bridg	ge C1 (P17	7 to P21)													
1210	0-3000	TTA Stage 1 - Close 2 Iane (1 & 2) > Open 2 Iane (3 & 4)	6	26-Dec-18	02-Jan-19					TTA Stage	1 - Close	2 lane (1 &	2) > 0	pen 2 Iane	e (3 & 4)
1210	0-3120	Stage 1 - Installation of temporary post & main beam (P17-P21)	24	03-Jan-19	30-Jan-19	-			L					Stage 1 - I	nstallation of t
1210	0-3240	Stage 1 - Installation of secondary beam & roof and side noise panel (P17-P21)	28	17-Jan-19	21-Feb-19	-									
12.2 -	Viaduct	Planters & Maintenance Access			,										
West	Bound B	rigde Between F2 to C4 (P40 to P28)													
1220	0-1000	Bridge F2C (F3-F5) - Construct planter wall (52m)	14	31-Jan-19	19-Feb-19								└╼┢		
East I	Bound Br	rigde Between F3 to E1 (P43 to P17) (Land Side) (parapet mould 2&3)													
1220	0-2000	TTA Stage 1 - Close 2 Iane (1 & 2); Open 2 Iane (3 & 4); for traffic from Bridge F2A to E	6	26-Dec-18*	02-Jan-19					TTA Stage	1 - Close	2 lane (1 &	2); Op	en 2 Iane	(3 & 4); for traf
													1		
1220	0-2040	Bridge F1A to E - Removal of existing asphalt	4	03-Jan-19	07-Jan-19					Bric	lge F1A to	E - Remov	al of ex	isting asp	halt
	D-2040 D-2080	Bridge F1A (F3-D12) - Preparation works; drill holes/clean couplers for starter	4 10	03-Jan-19 08-Jan-19	07-Jan-19 18-Jan-19					Bric	lge F1A to			0 1	halt paration works
1220										Bric	lge F1A to			0 1	
1220 1220	0-2080	Bridge F1A (F3-D12) - Preparation works; drill holes/clean couplers for starter bars	10	08-Jan-19	18-Jan-19	-				Bric	lge F1A to			0 1	paration works
1220 1220 1220	D-2080 D-2120	Bridge F1A (F3-D12) - Preparation works; drill holes/clean couplers for starter bars Bridge F1A (F3-D12) - Construction of inner parapet (88.4m)	10 21	08-Jan-19 15-Jan-19	18-Jan-19 11-Feb-19	-			-	Bric	lge F1A to	Bridge F1	A (F3-	012) - Pre	paration works
1220 1220 1220 1220	D-2080 D-2120 D-2160	<ul> <li>Bridge F1A (F3-D12) - Preparation works; drill holes/clean couplers for starter bars</li> <li>Bridge F1A (F3-D12) - Construction of inner parapet (88.4m)</li> <li>Bridge F1A (F3-D12) - Construct planter wall (88.4m)</li> <li>Bridge D2 (D6-D4) - Preparation works; drill holes/clean couplers for starter</li> </ul>	10 21 21	08-Jan-19 15-Jan-19 26-Jan-19	18-Jan-19 11-Feb-19 22-Feb-19				-1	Bric	lge F1A to	Bridge F1	A (F3-	012) - Pre	paration works Bridge F
1220 1220 1220 1220 1220	D-2080 D-2120 D-2160 D-2680	Bridge F1A (F3-D12) - Preparation works; drill holes/clean couplers for starter bars         Bridge F1A (F3-D12) - Construction of inner parapet (88.4m)         Bridge F1A (F3-D12) - Construct planter wall (88.4m)         Bridge D2 (D6-D4) - Preparation works; drill holes/clean couplers for starter bars	10 21 21 10	08-Jan-19 15-Jan-19 26-Jan-19 08-Jan-19	18-Jan-19 11-Feb-19 22-Feb-19 18-Jan-19	-				Bric		Bridge F1	A (F3-	012) - Pre	paration works Bridge F aration works; d
1220 1220 1220 1220 1220 1220	D-2080 D-2120 D-2160 D-2680 D-2720	Bridge F1A (F3-D12) - Preparation works; drill holes/clean couplers for starter bars         Bridge F1A (F3-D12) - Construction of inner parapet (88.4m)         Bridge F1A (F3-D12) - Construct planter wall (88.4m)         Bridge D2 (D6-D4) - Preparation works; drill holes/clean couplers for starter bars         Bridge D2 (D6-D4) - Onstruction of inner parapet (120m)	10 21 21 10 21	08-Jan-19 15-Jan-19 26-Jan-19 08-Jan-19 15-Jan-19	18-Jan-19 11-Feb-19 22-Feb-19 18-Jan-19 11-Feb-19	-				Bric	lge F1A to	Bridge F1	A (F3-I ? (D6-D	0 - Pre 012) - Pre	paration works Bridge F aration works; d

 Actual Level of Effort Actual Work

 Milestone •

#### Contract HY/2009/19 Three Months Rolling Programme (20.Dec.2018 to 20.Mar.2019)

019							
ту 17	24		02		arch 17	24	April
17	24		03	10 Bridge	C5 (P32-D1		31 / ruction of
		1 J		Ū	·	,	
							1
of tempo	rary pos	st & n	nain be	eam (P17	-P21)		
	Stano 1	- Inet	allatio	n of seco	ndary bear	n & roof an	d side noi
、							
📃 Brid	dge F20	C (F3	-F5) -	Construc	t planter w	all (52m)	
	•		,			. ,	
traffic from	m Bridg	e F2/	A to E				
		L					
rks; drill	holes/c	lean o	couple	ers for sta	rter bars		
eF1A(F	3-D12)	- Cor	nstruct	ion of inn	er parapet	(88.4m)	
	Bridge	F1A	(F3-D	12) - Cor	struct plan	ter wall (8	8.4m)
o: drill bo	-		-	for starte	-	,	
s, unin no			upiers		I Dais		
e D2 (D6	6-D4) - (	Const	ructio	n of inner	parapet (1	20m)	L
	Bridge	D2 (	D6-D4	I) - Const	ruct plante	wall (120	m)
Proporati	-				-		
reparatio		s, un	II NOIE	s/crean c	ouplers for	Starter Dar	5
				Bridge D	1 (D4-D1) -	Construct	on of inne
							1
					Page	4 of 4	
