CONTRACT NO: HK/2015/01

WANCHAI DEVELOPMENT PHASE II AND CENTRAL WANCHAI BYPASS SAMPLING, FIELD MEASUREMENT AND TESTING WORK (STAGE 3)

ENVIRONMENTAL PERMIT NO. EP-376/2009, FURTHER ENVIRONMENTAL PERMITS NO. FEP-01/376/2009 AND FEP-02/376/2009

QUARTERLY ENVIRONMENTAL MONITORING AND AUDIT REPORT

- NOV 2017 TO JAN 2018 -

CLIENTS:

Civil Engineering and Development Department PREPARED BY:

Lam Geotechnics Limited

11/F Centre Point 181-185 Gloucester Road, Wanchai, H.K.

Telephone: (852) 2882-3939 Facsimile: (852) 2882-3331 E-mail: <u>info@lamenviro.com</u>

Website: http://www.lamenviro.com

CHECKED BY:

Raymond Dai

Environmental Team Leader

DATE:

2| February 2018



Ref.: AACWBIECEM00 0 10211L.18

21 February 2018

By Post and Fax (2691 2649)

AECOM Asia Company Limited 11/F Tower 2 Grand Central Plaza 138 Shatin Rural Committee Road Shatin New Territories Hong Kong

Attention: Mr. Conrad Ng

Dear Mr. Ng,

Re: Contract No. HK/2015/01

Wan Chai Development Phase II - Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3)

Quarterly Environmental Monitoring and Audit Report (November 2017 to January 2018) for EP-376/2009

Reference is made to the Environmental Team's submission of the captioned Quarterly Environmental Monitoring and Audit (EM&A) Report received by e-mail on 21 February 2018 for our review and comment.

Please be informed that we have no adverse comment on the captioned submission.

Thank you for your attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,

David Yeung

Independent Environmental Checker

C.C.

CEDD

Attn: Mr. L K Tsang

by fax: 2577 5040

LAM

Attn: Mr. Raymond Dai

by fax: 2882 3331

AECOM

Attn: Mr. Francis Leong / Stephen Lai by fax: 2691 2649



TABLE OF CONTENTS

EX	ECUT	TIVE SUMMARY	3
1.	INTE	RODUCTION	5
	1.1 1.2	Scope of the ReportStructure of the Report	
2.	PRO	JECT BACKGROUND	6
	2.1 2.2 2.3 2.4	Background Scope of the Project and Site Description Project Organization and Contact Personnel Principal Work and Activities	6 7
3.	MON	IITORING REQUIREMENTS	9
	3.1. 3.2.	Noise MonitoringAir Quality Monitoring	9
4.	MON	IITORING RESULTS	12
	4.1. 4.2. 4.3.	Noise Monitoring Results Air Quality Monitoring Results Waste Monitoring Results	13
5.	COM	IPLIANCE AUDIT	17
	5.1. 5.2. 5.3. 5.4. 5.5.	Noise Monitoring	17 18 18
6.	COM	IPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION	19
7. PR	CUM OJEC	ULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT	
Q	CON	CLUSION	21



LIST OF TABLES

Table 1	Principal Work Activities in the reporting period
Table 2.1	Schedule 2 Designated Projects under this Project
Table 2.2	Contact Details of Key Personnel
Table 2.3	Principal Work Activities in the reporting period
Table 3.1	Noise Monitoring Stations
Table 3.2	Air Monitoring Stations
Table 4.1	Noise Monitoring Stations for Contract no. HK/2012/08
Table 4.2	Air Monitoring Station for Contract no. HK/2012/08
Table 4.3	Details of Waste Disposal for Contract no. HK/2012/08
Table 6.1	Cumulative Statistics on Complaints
Table 6.2	Cumulative Statistics on Successful Prosecutions

LIST OF FIGURES

Figure 2.1	Project Layout
Figure 2.2	Project Organization Chart
Figure 3.1	Locations of Environmental Monitoring Stations and Sensitive Receivers

LIST OF APPENDICES

Appendix 2.1	Environmental Mitigation Implementation Schedule
Appendix 3.1	Action and Limit Level
Appendix 4.1	Noise Monitoring Graphical Presentations
Appendix 4.2	Air Quality Monitoring Graphical Presentations
Appendix 5.1	Event Action Plans
Appendix 6.1	Complaint Log
Appendix 8.1	Construction Programme of Individual Contracts



EXECUTIVE SUMMARY

This is the Quarterly Environmental Monitoring and Audit (EM&A) Report – November 2017 to January 2018 specific for Environmental Permit no. EP-376/2009 and Further Environmental Permits no. FEP-01/376/2009 and FEP-02/376/2009. The EM&A report is prepared by the Environmental Team (ET) employed under Contract No. HK/2015/01 – Wan Chai Development Phase II and Central Wanchai Bypass – Sampling, Field Measurement and Testing Works (Stage 3). This report presents the environmental monitoring and audit findings and information during the period from 27th October 2017 to 26th January 2018. The cut-off date of reporting is at 26th of each reporting period

Construction Activities for the Reported Period

ii. During this reporting period, the principle work activities of the contract is included as follows:

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West</u>

Table 1 Principal Work Activities in the reporting period

November 2017	December 2017	January 2018
Drainage	Drainage	Drainage
Roadworks	Roadworks	Roadworks

Noise Monitoring

- iii. Noise monitoring was conducted at M1a Harbour Road Sports Centre.
- iv. With respect to the shift in major construction site portions at Wan Chai North, the noise monitoring station M1a Harbour Road Sports Centre was finely adjusted from East of Harbour Road Sports Centre to West of Harbour Road Sports Centre on 21 June 2016.
- v. With respect to the demolition of Ex-Harbour Road Sports Centre, the respective noise monitoring station M1a Harbour Road Sports Centre were finely adjusted on 16 and 25 May 2017 and thereafter to the Footbridge for Harbour Road Sports for noise monitoring.
- vi. Two limit exceedances were recorded on 3 and 22 November 2017 in November 2017 reporting month. After the investigation, the exceedances were concluded as non-project related.
- vii. Two limit exceedances were recorded on 4 and 11 December 2017 in December 2017 reporting month. After the investigation, the exceedances were concluded as non-project related.
- viii. Three limit exceedances were recorded on 29 December 2017, 16 and 23 January 2018 in January 2018 reporting month. After the investigation, the exceedances were concluded as non-project related.



Air Quality Monitoring

- ix. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted on every six days basis at CMA5b and CMA6a Contractor HK/2012/08 Site Office.
- x. Due to electricity supply interruption, the TSP monitoring in this reporting quarter were rescheduled as follow:
 - 24hr TSP monitoring at CMA5b was rescheduled from 11 Nov 2017 to 13 Nov 2017.
- xi. One 1hr TSP action level exceedance was recorded at CMA5b Pedestrian Plaza on 1 November 2017 in November 2017 reporting month. After the investigation, the exceedance was concluded as non-Project related.
- xii. Two 1hr TSP action level exceedances and one 1hr TSP limit level exceedance were recorded at CMA5b Pedestrian Plaza on 24 November 2017 in November 2017 reporting month. After the investigation, the exceedances were concluded as non-Project related.
- xiii. One 24hr TSP action level exceedance and two 1hr TSP action level exceedance were recorded at CMA5b Pedestrian Plaza on 11, 12 and 23 December 2017 in December 2017 reporting month. After the investigation, the exceedances were concluded as non-Project related.
- xiv. One 1-hr TSP action level exceedance was recorded at CMA5b Pedestrian Plaza on 29 December 2017 in January 2018 reporting month. After the investigation, the exceedances were concluded as non-Project related

Complaints, Notifications of Summons and Successful Prosecutions

xv. There was no environmental complaint recorded in this reporting quarter.

1. INTRODUCTION

1.1 Scope of the Report

1.1.1. Lam Geotechnics Limited (LGL) has been appointed take up the role as the Environmental Team (ET) under Environmental Permit no. EP-376/2009 and Further Environmental Permits no. FEP-01/376/2009 and FEP-02/376/2009 to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Wan Chai Development Phase II and Central-Wan Chai Bypass (Register No.: AEIAR-458/2008).

This report documents the finding of EM&A works for Environmental Permit (EP) no. EP-376/2009 and Further Environmental Permits no. FEP-01/376/2009 and FEP-02/376/2009, during the period 27th October 2017 to 26th January 2018. The cut-off date of reporting is the 26th of each reporting period.

1.2 Structure of the Report

Section 1 *Introduction* – details the scope and structure of the report.

Section 2 Project Background – summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.

Section 3 *Monitoring Requirements* – summarizes all monitoring parameters, monitoring locations, monitoring frequency, duration and action plan.

Section 4 Monitoring Results – summarizes the monitoring results obtained in the reporting period.

Section 5 Compliance Audit – summarizes the auditing of monitoring results, all exceedances environmental parameters.

Section 6 Complaints, Notification of summons and Prosecution – summarizes the cumulative statistics on complaints, notification of summons and prosecution

Section 7 Cumulative Construction Impact due to the Concurrent Projects – summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.

Section 8 Conclusion

2. PROJECT BACKGROUND

2.1 Background

2.1.1 Wan Chai Development phase II and Central-Wan Chai Bypass (hereafter called "the Project") are Designated Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Report for Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) has been approved on 11 December 2008.

2.2 Scope of the Project and Site Description

- 2.2.1. The design and construction of Wan Chai Development Phase II and Central Wanchai Bypass involves the construction and operation of primary and district distributor roads that is shown at <u>Figure 2.1.</u>
- 2.2.2. The key purpose of the study area encompasses the Wan Chai harbourfront area. The area starts at the boundary of Central Reclamation Phase III (CRIII) at the west and connects to the existing Hung Hing Road at the east. The scope of the project includes:
 - A dual 2-lane primary distributor road, Road P2, approximately 0.6km in length; and
 - Other new primary and district distributor roads connecting to the slip roads of the Central-Wan Chai Bypass with a total length of approximately 0.7km.
- 2.2.3. The project also contains various Schedule 2 DP that, under the EIAO, require Environmental Permits (EPs) to be granted by the DEP before they may be either constructed or operated. *Table 2.1* summarises the DP under this Project. *Figure 2.1* shows the locations of these Schedule 2 DP.

Table 2.1 Schedule 2 Designated Project under this Project

Item	Designated Project	EIAO Reference
DP2	Road P2 and other roads which are classified as	Schedule 2, Part I, A.1
	primary/district distributor roads	

2.2.4. The designated project work II (DP2) was awarded to China State-Build King Joint Venture HK/2012/08 – Wan Chai Development Phase II Central – Wan Chai Bypass at Wan Chai West as part of the Project works by the Civil Engineering and Development Department (CEDD). The construction work under EP-376/2009 by Contract no. HK/2012/08 was commenced on 13 May 2015.



2.3 Project Organization and Contact Personnel

- 2.3.1 Civil Engineering and Development Department and Highway Department are the overall project controllers for the Wan Chai Development Phase II and Central-Wan Chai Bypass respectively. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.3.2 The proposed project organization and lines of communication with respect to environmental protection works are shown in *Figure 2.2*. Key personnel and contact particulars are summarized in *Table 2.2*:

Table 2.2 Contact Details of Key Personnel

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Principal Resident Engineer	Mr. Frankie Fan	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3922 3388	3912 3010
China State- Build King	Contractor under Contract	Project Director	C. N. LAI	9106 5806	2877 1522
Joint Venture	no. HK/2012/08	Project Manager	Mr. Eddie Chung	9189 8118	
		Site Agent	Mr. George Cheung	9268 1918	
		Environmental Officer	Mr. James Ma	9130 9549	
Ramboll Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	3465 2888	3465 2899
Lam Geotechnics Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331
(For Enquiry)					



2.4 Principal Work and Activities

2.4.1 During this reporting period, the principle work activities of the contract is included as follows:

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West</u>

Table 2.3 Principal Work Activities in the reporting period

November 2017	December 2017	January 2018
Drainage	Drainage	Drainage
Roadworks	Roadworks	Roadworks

2.4.2 Implementation status of the recommended mitigation measures during this reporting period is presented in *Appendix 2.1*.

3. MONITORING REQUIREMENTS

3.1. Noise Monitoring

NOISE MONITORING STATION

3.1.1. The noise monitoring station for the Project is listed and shown in *Table 3.1* and *Figure 3.1*.
Appendix 3.1 shows the established Action/Limit Levels for the monitoring works.

Table 3.1 Noise Monitoring Station

District	Station	Description
Wan Chai	M1a	Footbridge for Ex-Harbour Road Sports Centre

NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 3.1.2. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (Leq). Leq (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods, Leq (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. Supplementary information for data auditing, statistical results such as L10 and L90 shall also be obtained for reference.
- 3.1.3. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
 - One set of measurements between 0700 and 1900 hours on normal weekdays.

MONITORING EQUIPMENT

- 3.1.4. As referred to in the Technical Memorandum ™ issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.
- 3.1.5. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.2. Air Quality Monitoring

AIR QUALITY MONITORING STATIONS

3.2.1. The air monitoring stations for the Project are listed and shown in *Table 3.2* and *Figure 3.1*. *Appendix 3.1* shows the established Action/Limit Levels for the monitoring works.

Table 3.2 Air Quality Monitoring Stations

Station ID Monitoring Location	
CMA5b	Pedestrian Plaza
CMA6a	WDII PRE Site Office

AIR MONITORING PARAMETERS, FREQUENCY AND DURATION

- 3.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 3.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.
- 3.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.

SAMPLING PROCEDURE AND MONITORING EQUIPMENT

- 3.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:
 - 0.6 1.7 m³ per minute adjustable flow range;
 - Equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
 - Installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
 - Capable of providing a minimum exposed area of 406 cm2;
 - Flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
 - Equipped with a shelter to protect the filter and sampler;
 - Incorporated with an electronic mass flow rate controller or other equivalent devices;



Lam Geotechnics Limited

Contract No. HK/2015/01 Wan Chai Development Phase II and Central Wanchai Bypass - Sampling, Field Measurement and Testing Works (Stage 3) Quarterly EM&A Report (Nov 2017- Jan 2018)

- Equipped with a flow recorder for continuous monitoring;
- Provided with a peaked roof inlet;
- Incorporated with a manometer;
- Able to hold and seal the filter paper to the sampler housing at horizontal position;
- · Easily changeable filter; and
- Capable of operating continuously for a 24-hour period.
- 3.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

LABORATORY MEASUREMENT / ANALYSIS

- 3.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.
- 3.2.8. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.
- 3.2.9. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.
- 3.2.10. All the collected samples shall be kept in a good condition for 6 months before disposal.

4. MONITORING RESULTS

- 4.0.1. The environmental monitoring will be implemented based on the division of works areas of the designed project managed under the contract with FEP applied by contractor. Overall layout showing work areas of various contracts, latest status of work commencement and monitoring stations is shown in *Figure 2.1* and *Figure 3.1*. The monitoring results are presented in according to the Individual Contract(s).
- 4.0.2. In the reporting period, the concurrent contract is:
 - Contract no. HK/2012/08 Wan Chai Development Phase II Central Wan Chai Bypass at Wan Chai West.

4.1. Noise Monitoring Results

- 4.1.1 Noise monitoring for project works under EP-376/2009 was commenced on 19 May 2015.
- 4.1.2 The proposed division of noise monitoring station is summarized in *Table 4.1* below.

Table 4.1 Noise Monitoring Station for Contract no. HK/2012/08

Location ID	District	Description
M1a	Wan Chai	Footbridge for Ex-Harbour Road Sports Centre

4.1.3 Two limit level exceedances were recorded on 3 and 22 November 2017 in November 2017 reporting month.

After the investigation, no construction work under EP-376/2009 was conducted by Contract HK/2012/08 on 3 November 2017 around the concerned location during the time of measurement while non WDII-CWB excavation works immediately next to the monitoring station was observed as the major noise contribution during monitoring. As such, the exceedance was considered as non-Project related to Contract HK/2012/08.

After the investigation, no construction work under EP-376/2009 was conducted by Contract HK/2012/08 on 22 November 2017 around the concerned location during the time of measurement while non WDII-CWB breaking works immediately next to the monitoring station was observed as the major noise contribution during monitoring. As such, the exceedance was considered as non-Project related to Contract HK/2012/08.

4.1.4 Two limit level exceedances were recorded on 4 and 11 December 2017 in December 2017 reporting month.



After the investigation, no construction work under EP-376/2009 was conducted by Contract HK/2012/08 on 4 December 2017 around the concerned location during the time of measurement while non WDII-CWB excavation works immediately next to the monitoring station was observed as the major noise contribution during monitoring. As such, the exceedance was considered as not related to Project works under Contract HK/2012/08.

After the investigation, no construction work under EP-376/2009 was conducted by Contract HK/2012/08 on 11 December 2017 around the concerned location during the time of measurement while non WDII-CWB breaking works next to the monitoring station was observed as the major noise contribution during monitoring. As such, the exceedance was considered as not relate to Project works under HK/2012/08.

4.1.5 Three limited level exceedances were recorded on 29 December 2017, 16 and 23 January 2018 in January 2018 reporting month.

After the investigation, no construction work under EP-376/2009 was conducted by Contract HK/2012/08 on 29 December 2017 around the concerned location during the time of measurement while non WDII-CWB excavation works immediately next to the monitoring station was observed as the major noise contribution during monitoring. As such, the exceedance was considered as not related to Project works under Contract HK/2012/08.

After the investigation, no construction work under EP-376/2009 was conducted by Contract HK/2012/08 on 16 January 2018 around the concerned location during the time of measurement while non WDII-CWB breaking works next to the monitoring station was observed as the major noise contribution during monitoring. As such, the exceedance was considered as not relate to Project works under HK/2012/08.

After the investigation, no construction work under EP-376/2009 was conducted by Contract HK/2012/08 on 23 January 2018 around the concerned location during the time of measurement while non WDII-CWB breaking works next to the monitoring station was observed as the major noise contribution during monitoring. As such, the exceedance was considered as not relate to Project works under HK/2012/08.

4.1.6 The noise monitoring results measured in this reporting period are reviewed and summarized.
Details of continuous noise monitoring results and graphical presentation can be referred to
Appendix 4.1

4.2. Air Quality Monitoring Results

4.2.1 Air Quality monitoring for project works under EP-376/2009 was commenced on 16 May 2015.

4.2.2 The proposed division of air quality monitoring stations are summarized in *Table 4.2* below.

Table 4.2 Air Quality Monitoring Station for Contract no. HK/2012/08

Station	Description
CMA5b	Pedestrian Plaza
CMA6a	WDII PRE Site Office

4.2.3 One 1hr TSP action level exceedance was recorded at CMA5b – Pedestrian Plaza on 1 November 2017 in November 2017 reporting month.

Road and drains works for P2 road was undertaken by the Contractor of HK/2012/08 around the monitoring location on the monitoring date and no particular observation regarding air quality impact was observed during sampling. Nevertheless, non WDII-CWB Project construction activities was observed opposite to the monitoring station on the monitoring date. Meanwhile, it was reported that the ambient air quality was adversely affected by accumulation of air pollutant influenced by the meteorological condition on the monitoring date. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality condition. Nevertheless, the Contractor of HK/2012/08 was reminded to provide regularly dust suppression measures if any potential dust generating operation around the concerned location would be required to avoid any potential cumulative air quality impact.

4.2.4 Two 1hr TSP action level exceedances and one 1hr TSP limit level exceedances was recorded at CMA5b – Pedestrian Plaza on 24 November 2017 in November 2017 reporting month.

Road and drains works for P2 road was undertaken by the Contractor of HK/2012/08 around the monitoring location on the monitoring date and no particular observation regarding air quality impact was observed during sampling. Nevertheless, non WDII-CWB Project construction activities was observed opposite to the monitoring station on the monitoring date. Meanwhile, according to the EPD monitoring record, highest pollutant concentration was recorded during the monitoring date at Causeway Bay monitoring station across a seven days period. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality condition. Nevertheless, the Contractor of HK/2012/08 was reminded to provide regularly dust suppression measures if any potential dust generating operation around the concerned location would be required to avoid any potential cumulative air quality impact.



4.2.5 One 24hr TSP action level exceedance and one 1hr TSP action level exceedance were recorded at CMA5b – Pedestrian Plaza on 11 and 12 December 2017 in December 2017 reporting month.

Road and drains works for P2 road was undertaken by the Contractor of HK/2012/08 around the monitoring location on the monitoring date and no particular observation regarding air quality impact was observed during sampling. Meanwhile, non WDII-CWB Project construction activities was observed opposite to the monitoring station on the monitoring date. According to the EPD monitoring record, AQHI recorded at the Causeway Bay station was recorded as Lv4 - Lv7 on 11 December 2017 and recorded as Lv6 on 12 December 2017 during the monitoring period indicating the adverse ambient condition. In addition, similar elevation in TSP level were recorded across the same period on 11 December 2017 at other Project AQM stations including CMA6a at Wan Chai and CMA3a at Causeway Bay area suggesting overall air quality within the district was under influence of ambient pollutant. In view of the above, the exceedance was considered to be not related to the Project works under Contract HK/2012/08 and potentially contributed by ambient air quality condition. Nevertheless, the Contractor of HK/2012/08 was advised to strengthen the overall dust suppression control measures to ensure all dusty surface are dampened to avoid potential dust emission.

4.2.6 One 1hr TSP action level exceedances was recorded at CMA5b – Pedestrian Plaza on 23 December 2017 in December 2017 reporting month.

Road and drains works for P2 road was undertaken by the Contractor of HK/2012/08 around the monitoring location on the monitoring date and no particular observation regarding air quality impact was observed during sampling. Meanwhile, non WDII-CWB Project excavation material handling was observed opposite to the monitoring station on the monitoring date. In addition, elevated PM2.5 and PM10 level were recorded at the EPD Causeway Bay monitoring station across the monitoring period suggesting the meteorological condition at the time of monitoring may not favor the dispersion of ambient air pollutant within the district and hence affecting the air quality. In view of the above, the exceedance was considered to be not related to the Project works under Contract HK/2012/08 and potentially contributed by ambient air quality condition. Nevertheless, the Contractor of HK/2012/08 was advised to strengthen the overall dust suppression control measures to ensure all dusty surface are dampened to avoid potential dust emission.

4.2.7 One 1hr TSP action level exceedance were recorded at CMA5b – Pedestrian Plaza on 29 December 2017 in January 2018 reporting month.

Road and drains works for P2 road was undertaken by the Contractor of HK/2012/08 around the monitoring location on the monitoring date and no particular observation regarding air quality impact was observed during sampling. Meanwhile, non WDII-CWB Project construction works was observed opposite to the monitoring station on the monitoring date. In

view of the above, the exceedance was considered to be not related to the Project works under Contract HK/2012/08 and potentially contributed by ambient air quality condition and nearby traffic exhaust. Nevertheless, the Contractor of HK/2012/08 was advised to strengthen the overall dust suppression control measures to ensure all dusty surface are dampened to avoid potential dust emission.

4.2.8 The air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in <u>Appendix 4.2.</u>

4.3. Waste Monitoring Results

4.3.1 No Inert and Non-inert C&D wastes disposed in this reporting period. Details of the waste flow table are summarized in *Table 4.3*.

Table 4.3 Details of Waste Disposal for Contract no. HK/2012/08

Waste Type	Quantity this quarter	Cumulative Quantity- to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m3	NIL	NIL	NIL
Inert C&D materials recycled, m3	NIL	NIL	NIL
Non-inert C&D materials disposed, m3	NIL	NIL	NIL
Non-inert C&D materials recycled, m3	NIL	NIL	NIL
Chemical waste disposed, kg	NIL	NIL	NIL

5. COMPLIANCE AUDIT

5.0.1. The Event Action Plan for construction noise and air quality are presented in Appendix 5.1.

5.1. Noise Monitoring

- 5.1.1 Two limit level exceedances were recorded on 3 and 22 November 2017 in November 2017 reporting month. After the investigation, the exceedances were concluded as non-project related.
- 5.1.2 Two limit level exceedances were recorded on 4 and 11 December 2017 in December 2017 reporting month. After the investigation, the exceedances were concluded as non-project related.
- 5.1.3 Three limit exceedances were recorded on 29 December 2017, 16 and 23 January 2018 in January 2018 reporting month. After the investigation, the exceedances were concluded as non-project related.

5.2. Air Quality Monitoring

- 5.2.1 One 1hr TSP action level exceedance was recorded at CMA5b Pedestrian Plaza on 1 November 2017 in November 2017 reporting month. After the investigation, the exceedance was concluded as non-project related.
- 5.2.2 Two 1hr TSP action level exceedances and one 1hr TSP limit level exceedances was recorded at CMA5b Pedestrian Plaza on 24 November 2017 in November 2017 reporting month. After the investigation, the exceedance was concluded as non-project related.
- 5.2.3 One 24hr TSP action level exceedance and two 1hr TSP action level exceedance were recorded at CMA5b – Pedestrian Plaza on 11, 12 and 23 December 2017 in December 2017 reporting month. After the investigation, the exceedances were concluded as non-Project related.
- 5.2.4 One 1-hr TSP action level exceedance was recorded at CMA5b Pedestrian Plaza on 29 December 2017 in January 2018 reporting month. After the investigation, the exceedances were concluded as non-Project related.

5.3. Site Audit

- 5.3.1 There was no non-compliance from the site audits in the reporting period. During environmental site inspections conducted during the reporting period, minor deficiencies were noted.
- 5.4. Review of the Reasons for and the Implications of Non-compliance
- 5.4.1 There was no non-compliance from the site audits in the reporting period.
- 5.5. Summary of action taken in the event of and follow-up on non-compliance
- 5.5.1 There was no particular action taken since no project-related non-compliance was recorded from the site audits and environmental monitoring in the reporting period.

6. COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION

- 6.0.1. No environmental complaint received in this reporting quarter.
- 6.0.2. The details of cumulative complaint log and summary of complaints are presented in *Appendix* 6.1.
- 6.0.3. No notification of summons or prosecution was received in the reporting period. Cumulative statistic on complaints and successful prosecutions are summarized in *Table 6.1* and *Table 6.2* respectively.

Table 6.1 Cumulative Statistics on Complaints

Reporting Period	No. of Complaints
Commencement works (May 2015) to last reporting quarter	0
November 2017 to January 2018	0
Project-to-Date	0

Table 6.2 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this quarter (Offence Date)	Cumulative No. Project-to-Date	
Air	-	0	0	
Noise	-	0	0	
Water	-	0	0	
Waste	-	0	0	
Total	-	0	0	



7. CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS

- 7.0.1. According to the Condition 3.4 of the EP-376/2009, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) and Wan Chai Development Phase II Central Wan Chai Bypass at Wan Chai East (CWB Tunnel).
- 7.0.2. According to the Final EM&A report of Central Reclamation Phase III (CRIII) for Contract HK 12/02, the major construction activities were completed by end of January 2014 and no construction activities were undertaken thereafter and the water quality monitoring was completed in October 2011. As such, it is considered that there were no cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) undertaken by contractor HK12/02 in the reporting period.
- 7.0.3. According to the construction programme of Central-Wanchai Bypass at Wanchai West at the Central Reclamation Phase III area roadworks, back-filling, reinstatement of culvert K, drainage, trimming of rock level and reinstatement of planter at P1 Road were performed in January 2018 reporting month. As no project related exceedance were recorded during the reporting period, cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was considered as insignificant.
- 7.0.4. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activities under Wan Chai Development Phase II were road and drains construction and backfilling works at Wan Chai West and Wan Chai East. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were drainage works and ventilation building construction at Central; temporary reclamation removal and reinstatement works at Causeway Bay, road works at Victoria Park; bridge construction, approach ramp construction and building construction at North Point area in the reporting period. In addition, other non-Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects was observed undertaken at Wan Chai North and North Point area.
- 7.0.5. No significant air quality impact from construction activities was anticipated in the reporting period. Besides, no project related exceedance was recorded during air quality and noise environmental monitoring events in the reporting period. Thus, it is evaluated that the cumulative construction impact from the concurrent projects including Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) was insignificant.




8. CONCLUSION

- 8.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.
- 8.0.2. No non-compliance and no prosecutions were received during the reporting period.
- 8.0.3. Mitigation measures according to the environmental mitigation implementation schedule and the EIA were generally implemented by the Contractor in this reporting period. Environmental site audit was conducted by the Environmental Team and the Independent Environmental Checker and no cumulative environmental impact was identified in the reporting period. Hence, the EM&A programme was considered effective and shall be maintained.
- 8.0.4. The construction programmes of individual contracts are provided in *Appendix 8.1*.

Figure 2.1

Project Layout

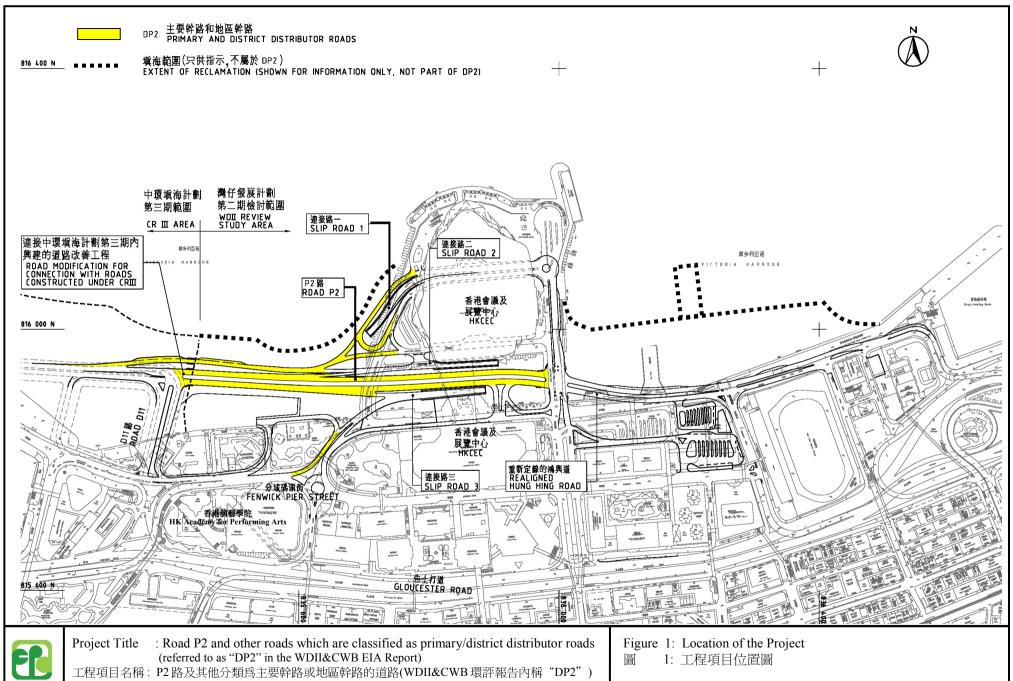

Environmental Permit No.: EP-376/2009 環境許可證編號 : EP-376/2009 (This figure was prepared based on Figure 1.2b of the WDII&CWB EIA report (Register No.: AEIAR-125/2008)) (本圖是根據 WDII&CWB 環評報告(登記冊編號 AEIAR-125/2008) 圖 1.2b 編制)

Figure 2.2

Project Organization Chart

Project Organization Chart




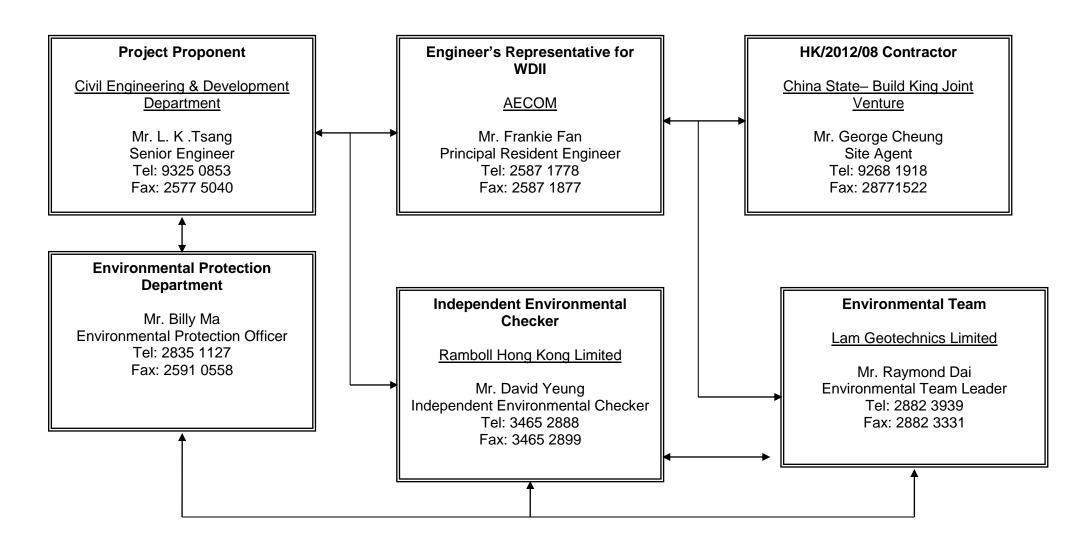


Figure 3.1

Locations of Environmental Monitoring Stations and Sensitive Recievers

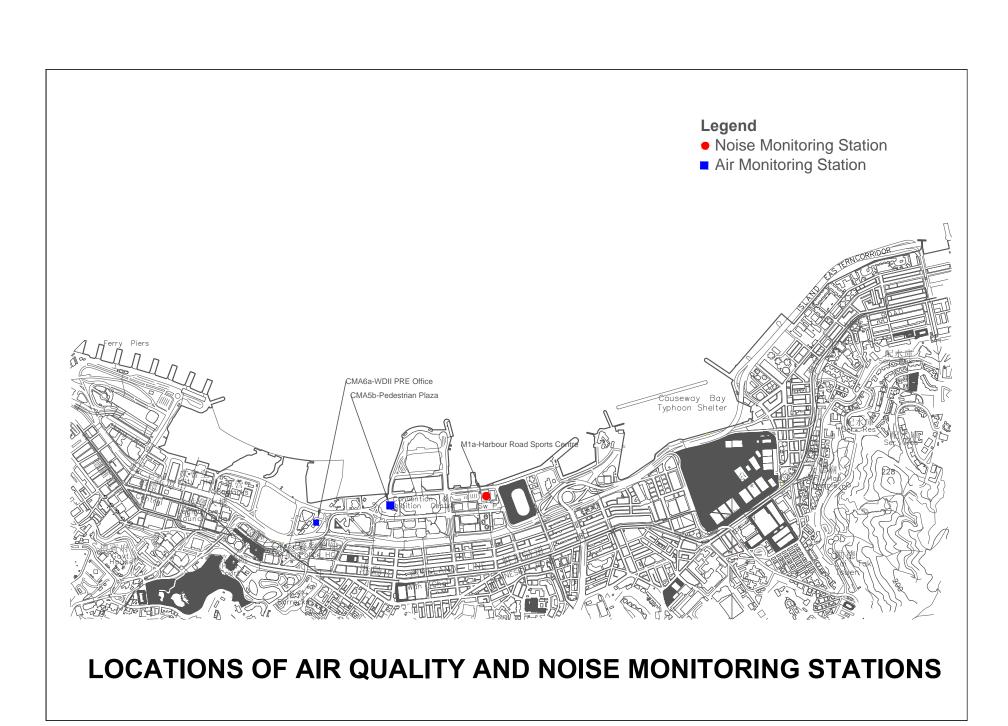

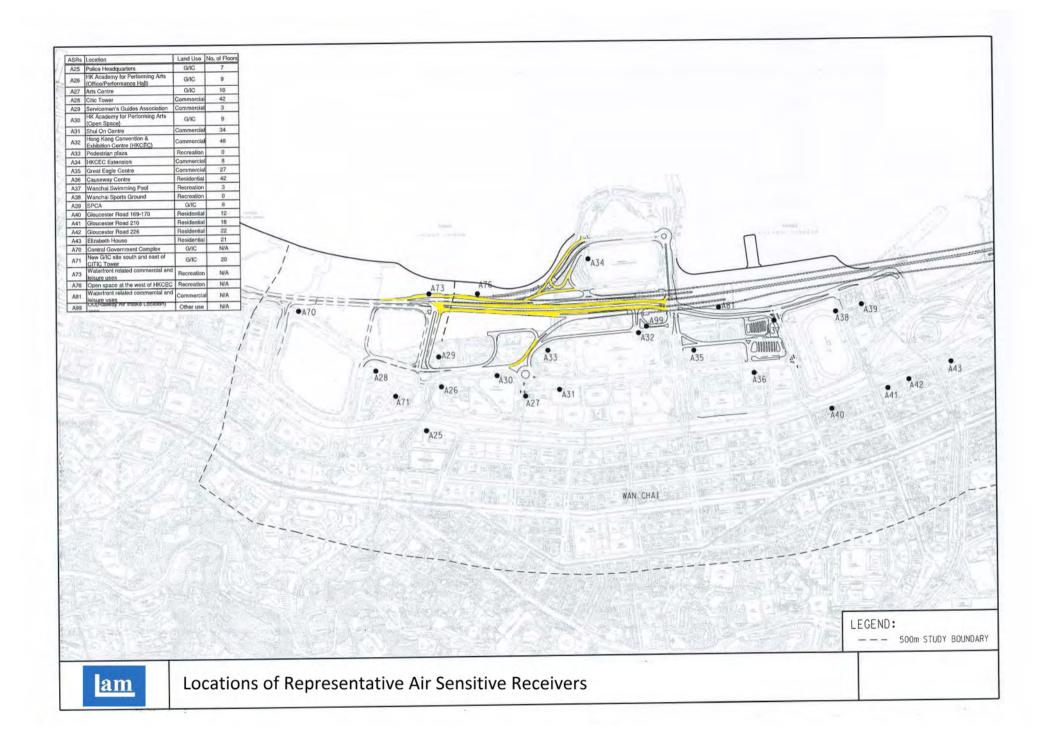

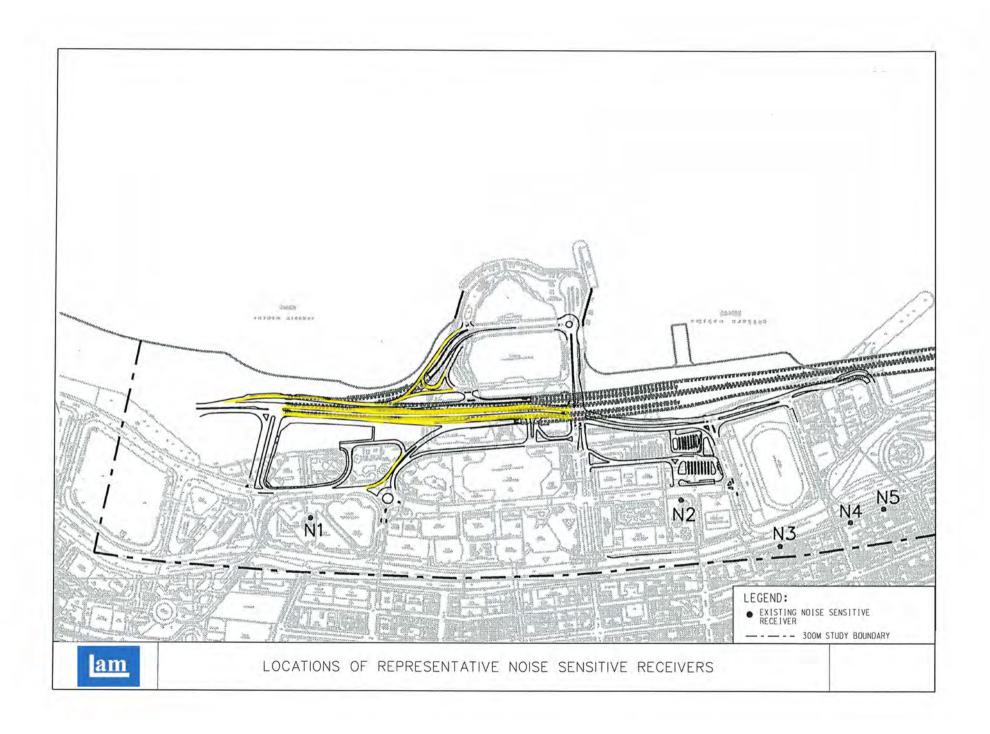

Appendix 2.1

Environmental Mitigation Implementation Schedule

Appendix A

Table A13.1 Implementation Schedule for Air Quality Control

Table A13.2 Implementation Schedule for Noise Control

Table A13.3 Implementation Schedule for Water Quality Control

Table A13.4 Implementation Schedule for Waste Management

Table A13.7 Implementation Schedule for Landscape and Visual

IMPLEMENTATION SCHEDULE OF THE PROPOSED MITIGATION MEASURES

Table A13.1 Implementation Schedule for Air Quality Control

EIA Ref	Environmental Protection Measures /	Location / Timing	Implementation	Implementation Status	Relevant Legislation	
	Mitigation Measures		Agent		and Guidelines	
Construction Phase						
For the Who	le Project					
S3.6.5	Four times a day watering of the work site with active operations.	Work site / during construction	Contractor	Implemented during Construction Stage	EIAO-TM	
S3.8.1	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimise cumulative dust impacts. Strictly limit the truck speed on site to below 10 km per hour and water spraying to keep the haul roads in wet condition; Watering during excavation and material handling; Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary; and Tarpaulin covering of all dusty vehicle loads transported to, from and between site	Work site / during construction	Contractor	Implemented during Construction Stage		

Table A13.2 Implementation Schedule for Noise Control

EIA Ref	Environmental Protection Measures /	Location / Timing	Implementation	Implementation Status	Relevant Legislation
	Mitigation Measures		Agent		and Guidelines
Construction	on Phase				
For the Wh	<u> </u>				
S4.9.4	Good Site Practice:	Work site / during	Contractor	Implemented during	EIAO-TM, NCO
	 Only well-maintained plant shall be 	construction		Construction Stage	
	operated on-site and plant shall be serviced				
	regularly during the construction program.				
	 Silencers or mufflers on construction 				
	equipment shall be utilized and shall be properly				
	maintained during the construction program.				
	 Mobile plant, if any, shall be sited as far 				
	away from NSRs as possible.				
	 Machines and plant (such as trucks) that 				
	may be in intermittent use shall be shut down				
	between works periods or shall be throttled down				
	to a minimum.				
	 Plant known to emit noise strongly in 				
	one direction shall, wherever possible, be				
	orientated so that the noise is directed away from				
	the nearby NSRs.				
	 Material stockpiles and other structures 				
	shall be effectively utilized, wherever				
	practicable, in screening noise from onsite				
	construction activities.				
	WDII Major Roads (Road P2)	T	1	T	T
S4.8.3 –	Use of quiet powered mechanical equipment,	Work site / during	Contractor	Implemented during	EIAO-TM, NCO
S4.8.4	movable noise	construction		Construction Stage	
	barrier and temporary noise barrier for the				
	following tasks:				
	 Temporary road diversion 				
	 Resurfacing 				
	 At-grade roadwork 				

Table A13.3 Implementation Schedule for Water Quality Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
Construction		I.	8		
For the Who					
S5.8	Construction Runoff and Drainage use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow; Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94; a sediment tank constructed from preformed individual cells of approximately 6 - 8 m3 capacity can be used for settling ground water prior to disposal; Oil interceptors shall be provided in the drainage system for the tunnels and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor shall have a bypass to prevent flushing during periods of heavy rain; precautions and actions to be taken when a rainstorm is imminent or forecast, and during or after rainstorms. Particular attention shall be paid to the control of any silty surface runoff during storm events; On-site drainage system shall be installed prior to the commencement of other construction activities. Sediment traps shall be	Work site / during construction	Contractor	Implemented during Construction Stage	ProPECC PN 1/94; WPCO (TM-DSS)

	installed in order to minimise the sediment loading of the effluent prior to discharge; All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge shall be adequately designed for the controlled release of storm flows. All sediment control measures shall be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage shall be reinstated to its original condition when the construction work is finished or the temporary diversion is no longer required.				
	 All fuel tanks and store areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity. Minimum distances of 100 m shall be maintained between the storm water discharges and the existing or planned WSD flushing water intakes during construction phase. 				
S5.8	Sewage from Construction Work Force Construction work force sewage discharges on site shall be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage shall be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor shall also be responsible for waste disposal and maintenance practices.	Work site / during construction	Contractor	Implemented during Construction Stage	ProPECC PN 1/94; WPCO (TM-DSS)

S5.8	Floating Debris and Refuse	Work site and	Contractor	Implemented during	WPCO
	Collection and removal of floating refuse shall	adjacent water /		Construction Stage	
	be performed at regular intervals on a daily	During the			
	basis. The contractor shall be responsible for	construction period.			
	keeping the water within the site boundary and				
	the neighbouring water free from rubbish.				
S5.8	Storm Water Discharges	Work site and	Contractor	Implemented during	WPCO
	Minimum distances of 100 m shall be	adjacent water		Construction Stage	
	maintained between the existing or planned	/ During the design			
	stormwater discharges and the existing or	and construction			
	planned WSD flushing water intakes.	period.			

Table A13.4 Implementation Schedule for Waste Management

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	Implementation Status	Relevant Legislation and Guidelines
Construction			Agent		and Guidennes
For the Wh					
S6.7.7	Good Site Practices	Work site / During	Contractor	Implemented during	
30.7.7	Recommendations for good site practices during	planning and	Contractor	Construction Stage	
	the construction activities include:	design stage, and		Construction Stage	
	nomination of an approved person, such	construction stage			
	as a site manager, to be responsible for good site	construction stage			
	practices, arrangements for collection and				
	effective disposal to an appropriate facility, of all				
	wastes generated at the site;				
	 training of site personnel in proper 				
	waste management and chemical waste handling				
	procedures;				
	 provision of sufficient waste disposal 				
	points and regular collection for disposal;				
	 appropriate measures to minimise 				
	windblown litter and dust during transportation				
	of waste by either covering trucks or by				
	transporting wastes in enclosed containers;				
	 regular cleaning and maintenance 				
	programme for drainage systems, sumps and oil				
	interceptors; and				
	a recording system for the amount of				
	wastes generated, recycled and disposed of				
~	(including the disposal sites).				
S.6.7.8	Waste Reduction Measures	Work site / During	Contractor	Implemented during	
	Recommendations to achieve waste reduction	planning and		Construction Stage	
	include:	design stage, and			
	Sort C&D waste from demolition of the	construction stage			
	existing waterfront structures to recover				
	recyclable portions such as metals.				

<u>EP-376/2009</u> EM&A Manual

	 Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal. Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force. Any unused chemicals or those with remaining functional capacity shall be recycled. Use of reusable non-timber formwork, such as in casting the tunnel box sections, to reduce the amount of C&D material. Proper storage and site practices to minimise the potential for damage or contamination of construction materials. Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. 				
S6.7.10	General Refuse General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D material. A collection area shall be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind blow' light material.	Work site / During the construction period	Contractor	Implemented during Construction Stage	Public Health and Municipal Services Ordinance (Cap. 132)

S6.7.11	Chemical Wastes After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals shall be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work site / During the construction period	Contractor	To be implemented at the corresponding stage of construction	Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
S6.7.12 – S6.7.13	Construction and Demolition Material C&D material shall be sorted on-site into inert C&D material (that is, public fill) and C&D waste. All the suitable inert C&D material shall be broken down to 250 mm in size for reuse as public fill in the WDII reclamation. C&D waste, such as wood, glass, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials. In order to monitor the disposal of public fill and C&D waste at public fill reception facilities and landfills, respectively, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team undertaking the environmental monitoring and audit work.	Work site / During the construction period	Contractor and Independent Environmental Checker	To be implemented at the corresponding stage of construction	DEVB TCW No.6/2010; ETWB TCW No. 33/2002; ETWB TCW No. 19/2005
	An Independent Environment Checker shall be responsible for auditing the results of the system.				
S6.7.14	Bentonite Slurry The disposal of residual used bentonite slurry shall follow the good practice guidelines stated	Work site / During the construction period	Contractor	To be implemented at the corresponding stage of construction	ProPECC PN 1/94

EP-376/2009 EM&A Manual in ProPECC PN 1/94 "Construction Site Drainage" and listed as follows: If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis. If the used bentonite slurry is intended to be disposed of through the public drainage system, it shall be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the Technical Memorandum of Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters. If the used bentonite slurry is intended

to be disposed to public fill reception facilities, it will be mixed with dry soil on site before

disposal.

Table A13.7 Implementation Schedule for Landscape and Visual

EIA Ref	Environmental Protection Measures /	Location / Timing	Implementation	Implementation Status	Relevant Legislation
	Mitigation Measures		Agent		and Guidelines
Construction	n Phase				
For the Who	le Project				
Table 10.5	CM1 Topsoil, where identified, shall be stripped	Work site / During	Contractor	Implemented during	EIAO TM
	and stored for re-use in the construction of the	Construction Phase		Construction Stage	
	soft landscape works, where practical.				
Table 10.5	CM2 Existing trees to be retained on site shall be	Work site / During	Contractor	Implemented during	EIAO TM
	carefully protected during construction.	Construction Phase		Construction Stage	
Table 10.5	CM3 Trees unavoidably affected by the works	Work site / During	Contractor	Implemented during	EIAO TM
	shall be transplanted where practical.	Construction Phase		Construction Stage	
Table 10.5	CM4 Compensatory tree planting shall be	Work site / During	Contractor	Implemented during	EIAO TM
	provided to compensate for felled trees.	Construction Phase		Construction Stage	
Table 10.5	CM5 Control of night-time lighting.	Work site / During	Contractor	Implemented during	EIAO TM
		Construction Phase		Construction Stage	
Table 10.5	CM6 Erection of decorative screen hoarding	Work site / During	Contractor	Implemented during	EIAO TM
	compatible with the surrounding setting.	Construction Phase		Construction Stage	
For DP2 – W	DII Major Roads (Road P2)				
Table 10.5	CM1 Topsoil, where identified, shall be stripped	Work site / During	Contractor	Implemented during	EIAO TM
	and stored for re-use in the construction of the	Construction Phase		Construction Stage	
	soft landscape works, where practical.			_	
Table 10.5	CM2 Existing trees to be retained on site shall be	Work site / During	Contractor	Implemented during	EIAO TM
	carefully protected during construction.	Construction Phase		Construction Stage	
Table 10.5	CM3 Trees unavoidably affected by the works	Work site / During	Contractor	Implemented during	EIAO TM
	shall be transplanted where practical.	Construction Phase		Construction Stage	
Table 10.5	CM4 Compensatory tree planting shall be	Work site / During	Contractor	Implemented during	EIAO TM
	provided to compensate for felled trees.	Construction Phase		Construction Stage	
Table 10.5	CM5 Control of night-time lighting.	Work site / During	Contractor	Implemented during	EIAO TM
		Construction Phase		Construction Stage	
Table 10.5	CM6 Erection of decorative screen hoarding	Work site / During	Contractor	Implemented during	EIAO TM
	compatible with the surrounding setting.	Construction Phase		Construction Stage	
				, and the second	

Operation Pl	Operation Phase						
For DP2 – W	For DP2 – WDII Major Roads (Road P2)						
Table 10.6,	OM1 Aesthetic design of buildings and road-	Work site / During	CEDD/HyD	To be implemented	ETWB TCW 2/2004		
Figure	related structures,	Design Stage and		during Operation Stage			
10.5.1-	including viaducts, vent buildings, subways,	Operation Phases					
10.5.5	footbridges						
	and noise barriers and enclosure.						
Table 10.6,	OM3 Buffer Tree and Shrub Planting to screen	Work site / During	CEDD/HyD	To be implemented	ETWB TCW 2/2004		
Figure	proposed roads	Design Stage and		during Operation Stage			
10.5.1-	and associated structures.	Operation Phases					
10.5.5							
Table 10.6,	OM5 Aesthetic streetscape design.	Work site / During	CEDD/HyD	To be implemented	ETWB TCW 2/2004		
Figure		Design Stage and		during Operation Stage			
10.5.1-		Operation Phases					
10.5.5							
Table 10.6,	OM6 Aesthetic design of roadside amenity areas	Work site / During	CEDD/HyD	To be implemented	ETWB TCW 2/2004		
Figure		Design Stage and		during Operation Stage			
10.5.1-		Operation Phases					
10.5.5							

Appendix 3.1

Action and Limit Level

Action and Limit Level

Action and Limit Level for Noise Monitoring

Time Period	Action Level	Limit Level
07:00 - 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A)


Notes: If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed. *The Limit level shall be 70 dB(A) and 65 dB(A) for educational institute during normal teaching periods and school examination periods, respectively.

Action and Limit Level for Air Monitoring

Monitoring Locations	1-hour TSP Level inµg/m3		24-hour TSP Level inµg/m3	
	Action Level	Limit Level	Action Level	Limit Level
CMA5b Pedestrian Plaza	339.7	500	209.9	260
CMA6a WDII PRE Site Office	333.0	500	207.1	260

Appendix 4.1


Noise Monitoring Graphical Presentations





Graphic Presentation of Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

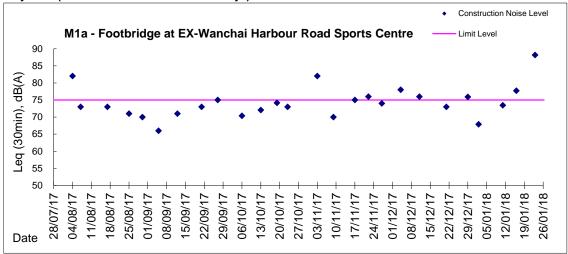


Appendix 4.2


Air Quality Monitoring Graphical Presentations



Graphic Presentation of 1 hour TSP Result for EP-376/2009

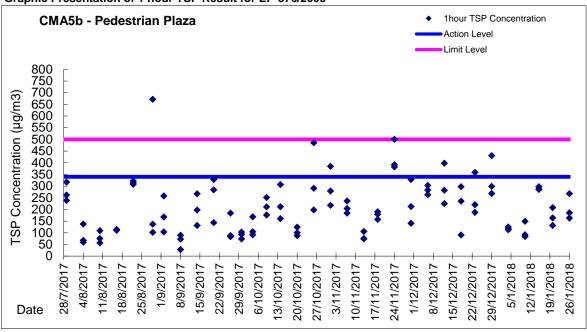



Graphic Presentation of 24 hour TSP Result for EP-376/2009

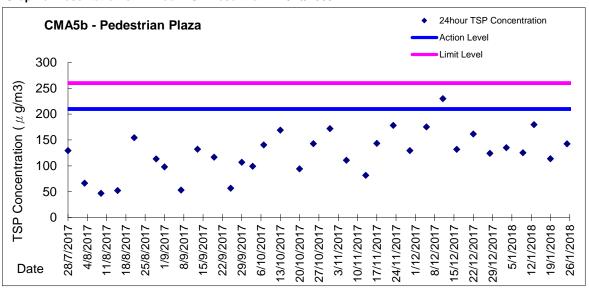




Graphic Presentation of 1 hour TSP Result for EP-376/2009

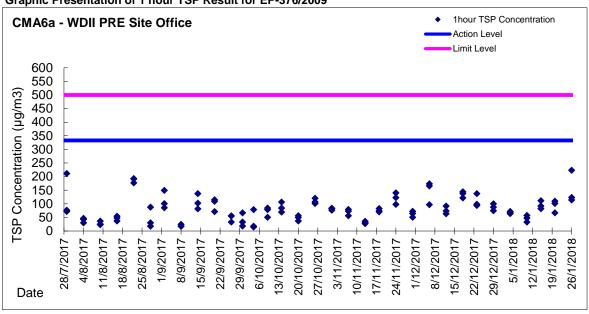



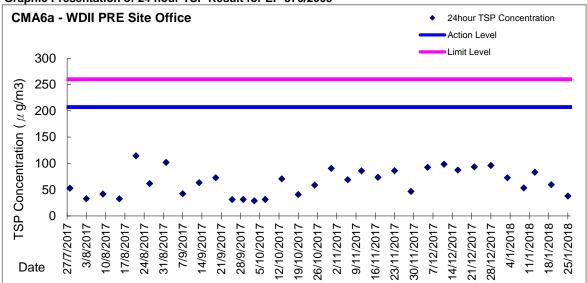

Appendix 5.1

Event Action Plans

Event/Action Plan for Construction Noise

EVENT		A	CTION	
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	 Notify ER, IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, ER and Contractor; Discuss with the IEC and Contractor on remedial measures required; Increase monitoring frequency to check mitigation effectiveness. (The above actions should be taken within 2 working days after the exceedance is identified) 	1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Advise the ER on the effectiveness of the proposed remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	 Confirm receipt of notification of failure in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified) 	Submit noise mitigation proposals to IEC and ER; Implement noise mitigation proposals. (The above actions should be taken within 2 working days after the exceedance is identified)



EVENT		AC	CTION	
	ET	IEC	ER	CONTRACTOR
Limit Level being exceeded	 Inform IEC, ER, Contractor and EPD; Repeat measurements to confirm findings; Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contractor's working procedures; 6. Discuss with the IEC, Contractor and ER on remedial measures required; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified) 	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. (The above actions should be taken within 2 working days after the exceedance is identified)	of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures;	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC and ER within 3 working days of notification; Implement the agreed proposals; Submit further proposal if problem still not under control; Stop the relevant portion of works as instructed by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)

Event / Action Dian for Construction Air Quality

FVENT	ACTION				
EVENT	ET	IEC	ER	CONTRACTOR	
ACTION LEVEL					
Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; Increase monitoring frequency to daily. (The above actions should be taken within 2 working days after the exceedance is identified)	Check monitoring data submitted by ET; Check Contractor's working method. (The above actions should be taken within 2 working days after the exceedance is identified)	Notify Contractor. (The above actions should be taken within 2 working days after the exceedance is identified)	Rectify any unacceptable practice; Amend working methods if appropriate (The above actions should be taken within 2 working days after the exceedance is identified)	
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Supervise Implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	Submit proposals for remedial to ER within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)	
LIMIT LEVEL					
Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. (The above actions should be taken within 2 working days after the exceedance is identified)	Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ER on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification 3. Implement the agreed proposals; Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)	
Exceedance for two or more consecutive samples	Notify IEC, ER, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring, (The above actions should be taken within 2 working days after the exceedance is identified)	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures.	Confirm receipt of notification of failure in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification 3. Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)	

Appendix 6.1

Complaint Log

Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					-	


Appendix 8.1

Construction Programme of Individual Contracts



CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central - Wan Chai Bypass at Wan Chai West

Page: 1 / 5

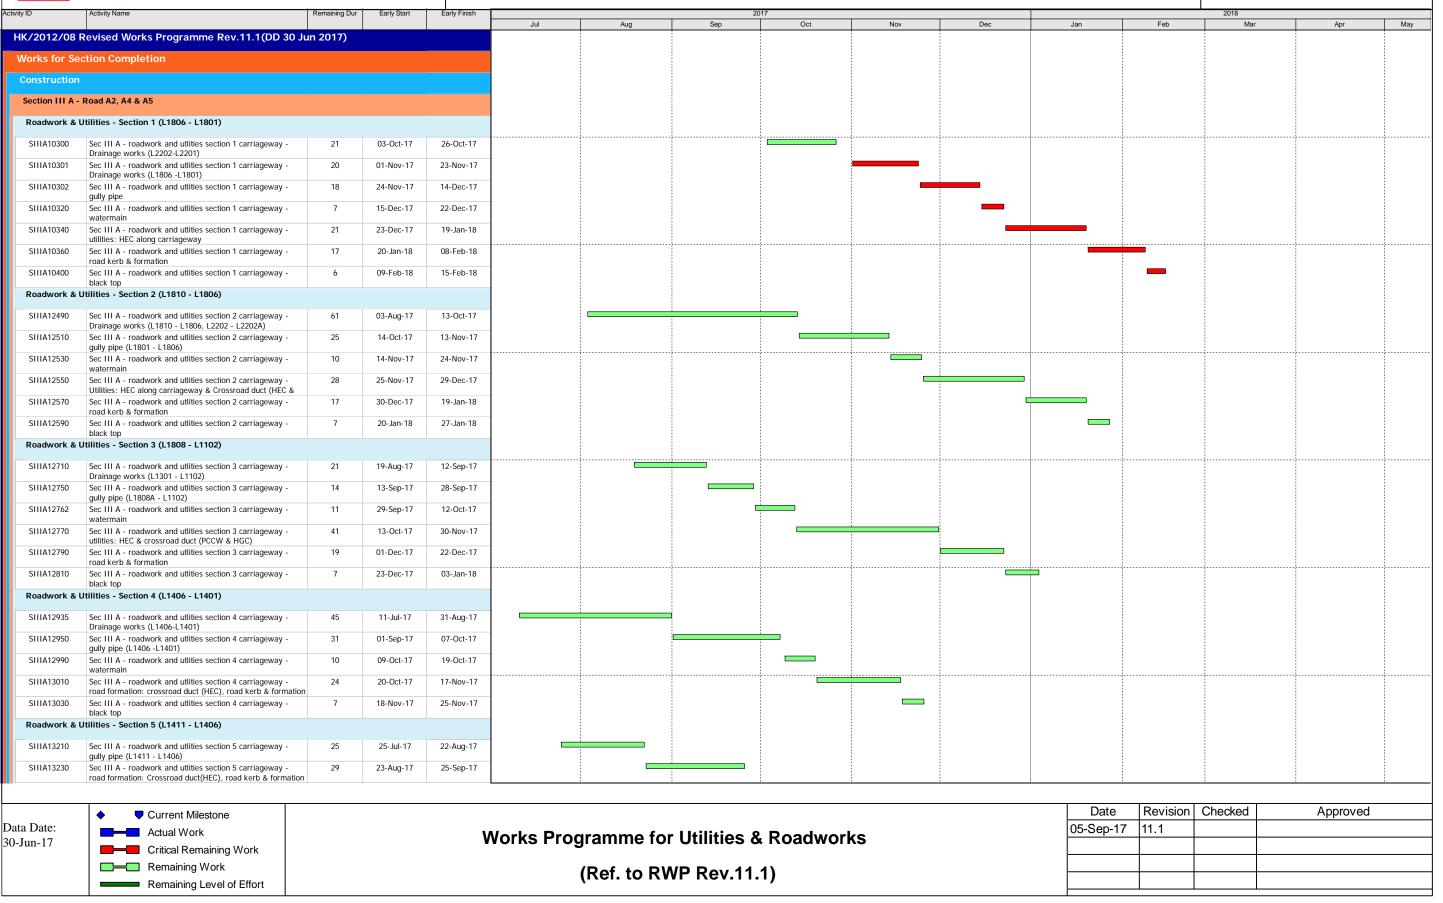



CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central - Wan Chai Bypass at Wan Chai West

Page: 2 / 5

	OHNAOTATE EEA							опаг Буразз с							
tivity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Jul	Aug	Sep 20	Oct Oct	Nov	Dec	Jan	Feb	2018 Mar	Apr	May
SIIIA13250	Sec III A - roadwork and utilities section 5 carriageway - black top	7	26-Sep-17	04-Oct-17											
Roadwork & l	Utilities - Section 6 (L1102 - L1411)														
SIIIA13372	Sec III A - roadwork and utilities section 6 carriageway - Backfilling of water channel adjacent culvert K bay 16	14	18-Aug-17	02-Sep-17			-								
SIIIA13373	Sec III A - roadwork and utilities section 6 carriageway -	20	24-Aug-17	15-Sep-17		_									
SIIIA13380	Backfilling of water channel from culvert K bay 16 to 20B Sec III A - roadwork and utilities section 6 carriageway -	9	16-Sep-17	26-Sep-17											
SIIIA13385	Removal of temporary water channel Sec III A - roadwork and utilities section 6 carriageway -	6	27-Sep-17	04-Oct-17			_	-			-				
SIIIA13389	Waterproofing for tunnel roof slab Sec III A - roadwork and utilities section 6 carriageway -	5	05-Oct-17	10-Oct-17				_							
SIIIA13395	Backfilling above tunnel roof slab Sec III A - roadwork and utilities section 6 carriageway -	9	11-Oct-17	20-Oct-17											
SIIIA13399	Drainage works (L1101-L1102) Sec III A - roadwork and utilities section 6 carriageway -	8	21-Oct-17	31-Oct-17											
SIIIA13430	gully pipe (L1101 -L1102) Sec III A - roadwork and utilities section 6 carriageway -	30	03-Aug-17	06-Sep-17											
SIIIA13444	gully pipe (Culvert L - L1411) Sec III A - roadwork and utilities section 6 carriageway -	7	07-Sep-17	14-Sep-17											
SIIIA13445	watermain Sec III A - roadwork and utilities section 6 carriageway -	14	15-Sep-17	30-Sep-17				1							
SIIIA13450	utilities: HEC , HGC, PCCW Sec III A - roadwork and utilities section 6 carriageway -	18	01-Nov-17	21-Nov-17				_							
SIIIA13470	road kerb & formation Sec III A - roadwork and utilities section 6 carriageway -	7	22-Nov-17	29-Nov-17											
Section V - Roa	black top														
Roadwork & U	Utilities										-			-	
Section 1 (L15															
SV12450		64	27-Jul-17	10-Oct-17	_										
	Sec V - Roadwork & Utilities Section 1 Carriageway - Gully pipe (L1903 - L1906, L1501-L1504)				_				1						
SV12460	Sec V - Roadwork & Utilities Section 1 Carriageway - Utilities (TCSS crossroad duct)		11-Oct-17	04-Nov-17						<u> </u>					
SV12490	Sec V - Roadwork & Utilities Section 1 Carriageway - Road kerb & formation		06-Nov-17	02-Dec-17				ļ							
SV12520	Sec V - Roadwork & Utilities Section 1 Carriageway - Black top	20	04-Dec-17	28-Dec-17											
SV12540	Sec V - Roadwork & Utilities Section 1 footpath - Watermain	14	06-Nov-17	21-Nov-17											
SV12570	Sec V - Roadwork & Utilities Section 1 footpath - utilities:TCSS	30	22-Nov-17	28-Dec-17											
SV12580	Sec V - Roadwork & Utilities Section 1 footpath - paving block	30	29-Dec-17	02-Feb-18											
Section 2 (L1	1510 - L1504)														
SV12602	Sec V - Roadwork & Utilities Section 2 Carriageway : Backfilling	7	18-Aug-17	25-Aug-17											
SV12603	Sec V - Roadwork & Utilities Section 2 Carriageway - Gully pipe (L1501 - L1507 & L1611 - L1609)	30	26-Aug-17	29-Sep-17		-									
SV12604	Sec V - Roadwork & Utilities Section 2 Carriageway : formation for access diversion	6	30-Sep-17	07-Oct-17			1								
SV12606	Sec V - Roadwork & Utilities Section 2 Carriageway: Divert access cross Zone B	0	09-Oct-17					•							
SV12610	Sec V - Roadwork & Utilities Section 2 Carriageway - Drainage Works L1507-L1504)	31	09-Oct-17	14-Nov-17											
SV12630	Sec V - Roadwork & Utilities Section 2 Carriageway - Drainage Works L1406A - L1406B	21	15-Nov-17	08-Dec-17						<u> </u>	-			†	
SV12665	Sec V - Roadwork & Utilities Section 2 Carriageway - Gully pipe (L1507-L1504, L1406A)	25	09-Dec-17	10-Jan-18							_				
SV12666	Sec V - Roadwork & Utilities Section 2 Carriageway - Utilities: HEC crossroad duct	11	11-Jan-18	23-Jan-18											
SV12670	Sec V - Roadwork & Utilities Section 2 Carriageway - Road kerb & formation	21	24-Jan-18	20-Feb-18							_				
SV12680	Sec V - Roadwork & Utilities Section 2 Carriageway - Black	20	21-Feb-18	15-Mar-18								_			
SV12690	top Sec V - Roadwork & Utilities Section 2 footpath - Drainage	25	09-Dec-17	10-Jan-18								 		 	+
SV12695	Works (L2104 - L2105) Sec V - Roadwork & Utilities Section 2 footpath - Watermain	18	11-Jan-18	31-Jan-18											
SV12700	Sec V - Roadwork & Utilities Section 2 footpath - utilities:	16	01-Feb-18	22-Feb-18											
	TCSS Sec V - Roadwork & Utilities Section 2 footpath - paving	18	23-Feb-18	15-Mar-18								_			
SV12740	See V - Roadwork & Othines Section 2 rootpath - paving									A CONTRACTOR OF THE CONTRACTOR	1	1	A CONTRACTOR OF THE CONTRACTOR		1



CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central - Wan Chai Bypass at Wan Chai West

Page: 3 / 5

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish				017					2018		
SIV12765	Sec V - Roadwork & Utilities Section 3 Carriageway -	25	16-Aug-17*	13-Sep-17	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
SIV12766	Demolish D wall Sec V - Roadwork & Utilities Section 3 Carriageway -	14	28-Sep-17	14-Oct-17		1 1 1 1 1 1									
SIV12810	Drainage Works (Culvert L - L1611) Sec V - Roadwork & Utilities Section 3 Carriageway - Gully	30	16-Oct-17	20-Nov-17											
SIV12815	pipe (Culvert L - L1611) Sec V - Roadwork & Utilities Section 3 Carriageway - Road	24	21-Nov-17	18-Dec-17											
SIV12820	kerb & formation Sec V - Roadwork & Utilities Section 3 Carriageway - Black	20	19-Dec-17	13-Jan-18											
SIV12840	Sec V - Roadwork & Utilities footpath - Drainage works	25	16-Oct-17	14-Nov-17											
SIV12844	(Culvert L - L2105) Sec V - Roadwork & Utilities Section 3 footpath - U channel	21	15-Nov-17	08-Dec-17						:					
SIV12850	Sec V - Roadwork & Utilities footpath - Watermain	21	15-Nov-17	08-Dec-17											
SIV12855	Sec V - Utilities: HEC (80m at site access) to MVB Plant Room - 1st stage excavation	10	15-Jul-17*	26-Jul-17											
SIV12857	Sec V - Utilities: HEC (80m at site access) to MVB Plant Room - 2nd stag excavation	10	08-Aug-17	18-Aug-17											
SIV12859	Sec V - Utilities: HEC (80m at site access) to MVB Plant Room - cabling	12	25-Aug-17	07-Sep-17											
SIV12860	Sec V - Roadwork & Utilities Section 3 footpath - Utilities: TCSS, HGC, PCCW)	39	09-Dec-17	26-Jan-18		; ; ; ; ; ;									
SIV12880	Sec V - Roadwork & Utilities Section 3 footpath - Paving block	22	27-Jan-18	24-Feb-18											
Section 4 (K1	106 - Culvert L)					 									
SIV12282	Sec V - Roadwork & Utilities Section 4 Carriageway - Drainage Works (K1311 - Culvert K, L1201, L1301)	31	16-Sep-17	23-Oct-17											
SIV12300	Sec V - Roadwork & Utilities Section 4 Carriageway - Gully pipe (K1106-Culvert K, K1201-Culvert K, L1201, L1301)	35	24-Oct-17	04-Dec-17											
SIV12305	Sec V - Roadwork & Utilities Section 4 Carriageway - Utilities : crossroad duct	14	05-Dec-17	20-Dec-17											
SIV12310	Sec V - Roadwork & Utilities Section 4 Carriageway - Road kerb & formation	24	02-Jan-18	29-Jan-18											
SIV12320	Sec V - Roadwork & Utilities Section 4 Carriageway - Black top	20	30-Jan-18	24-Feb-18		1 1 1 1 1									
SIV12360	Sec V - Roadwork & Utilities Section 4 Carriageway - watermain	15	21-Dec-17	10-Jan-18											
SIV12380	Sec V - Utilities: HEC (50m at water channel) to MVB plant room - Excavation	10	22-Aug-17	01-Sep-17											
SIV12400	Sec V - Utilities: HEC (50m at water channel) to MVB plant room - Cabling	9	08-Sep-17	18-Sep-17		1 1 1 1 1 1 1									
SIV12420	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : TCSS	21	11-Jan-18	03-Feb-18											
SIV12440	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : HGC & PCCW	8	21-Dec-17	02-Jan-18											
SIV12460	Sec V - Roadwork & Utilities Section 4 footpath - Paving block	22	05-Feb-18	05-Mar-18											
Section IV - S	ip Road 3														
Roadwork &	Utilities														
Section 1 (L1	6608 - L1601)														
SIV11750	Sec IV - Roadworks & Utilites at SR3 Section 1 Carriageway - Sewerage works	14	16-Sep-17	03-Oct-17				<u> </u>							
SIV11760	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L1607-L1601, L2004-L2005)		16-Sep-17	02-Nov-17					•						
SIV11762	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L2103-L2101)		03-Nov-17	27-Nov-17											
SIV11764	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Gully pipe (L1607-L1601, L2004-L2005)	25	28-Nov-17	28-Dec-17					•						
SIV11780	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Watermain	18	29-Dec-17	19-Jan-18											
SIV11800	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Utilities : TCSS crossroad duct	14	20-Jan-18	05-Feb-18											
SIV11830	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Road kerb & formation	24	06-Feb-18	08-Mar-18											
SIV11840	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Black top	11	09-Mar-18	21-Mar-18						_					
SIV11860	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - Drainage Works: future connection pipes	7	29-Dec-17	06-Jan-18		1 1 1 1 1 1				-					
SIV11880	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - watermain	/	08-Jan-18	15-Jan-18		1 1 1 1 1 1									
SIV11900	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - utilities: HEC & TCSS	39	16-Jan-18	05-Mar-18											
SIV11920	Sec IV - Roadwork & Utilities at SR3 Section 1 footpath - paving block	17	06-Mar-18	24-Mar-18											



CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central - Wan Chai Bypass at Wan Chai West

Page: 4 / 5

DUDLE	CHINA STATE - LEA	NDEK JOIN	I VENTURE	•	Central - Wan Chai Bypass at Wan Chai West													
Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Jul	Aug	Sep 20	017 Oct	Nov	Dec	Jan	Feb	2018 Mar	Apr	May			
Section 2 (L	2301 - L2103)				Jui	Aug	Зер	OCI	NOV	Dec	Jan	reb	ividi	Арі	iviay			
SIV11940	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Drainage Works (L2301-L2103)	- 21	23-Sep-17	18-Oct-17														
SIV11941	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Drainage Works (L608-L1609)	- 30	19-Oct-17	23-Nov-17										1				
SIV11942	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Gully pipe (L2301-L2013, L1608-L1609)	- 22	24-Nov-17	19-Dec-17										 				
SIV11960	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Watermain	- 10	20-Dec-17	03-Jan-18										, - - -				
SIV11970	Sec IV - Utilities: HEC (40m crossing) to MVB plant room - excavation	10	27-Jul-17	07-Aug-17														
SIV11975	Sec IV - Utilities: HEC (40m crossing) to MVB plant room - cabling	5	19-Aug-17	24-Aug-17														
SIV11980	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Utilities: TCSS crossroad duct)		04-Jan-18	19-Jan-18										 				
SIV12010	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Road kerb & formation		20-Dec-17	19-Jan-18										 				
SIV12020	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Black top	7	20-Jan-18	27-Jan-18										-				
SIV12040	Sec IV - Roadwork & Utilities at SR3 Section 2 footpath - Drainage Works: future connection pipes	7	04-Jan-18	11-Jan-18														
SIV12060	Sec IV - Roadwork & Utilities at SR3 Section 2 footpath - utilities: TCSS	25	12-Jan-18	09-Feb-18										 				
SIV12080	Sec IV - Roadwork & Utilities at SR3 Section 2 footpath - paving block /H1.6 - L2301)	21	10-Feb-18	09-Mar-18					1 1 1 1 1 1					; ; ; ;				
									1 1 1 1									
SIV12100	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M/H1.7 - L2301)		19-Oct-17	24-Nov-17										<i>,</i>				
SIV12102	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: Demolish seawall		23-Sep-17	17-Oct-17														
SIV12103	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: ELS		18-Oct-17	30-Oct-17										 				
SIV12104 SIV12105	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: Construct manhole & pipes Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -		31-Oct-17 12-Dec-17	11-Dec-17 27-Dec-17					 					; ; ; ;				
SIV12105	M1.7-M1.6: backfilling & divert EVA Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -		28-Dec-17	30-Jan-18														
SIV12120	Drainage Works (M1.6-C1.1-C1.2): Construct MH and pipes Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -		31-Jan-18	13-Feb-18										 				
SIV12122	Drainage Works (M1.6-C1.1-C1.2): Backfilling & shift lane Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway		14-Feb-18	28-Feb-18														
SIV12138	Drainage Works (M1.6-C1.1-C1.2): Construct MH C1.2 Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway	38	20-Jul-17*	01-Sep-17)											
SIV12140	-Utilities: HEC to MVB Plant room - cabling Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	- 30	25-Nov-17	02-Jan-18					_					1				
SIV12150	Gully pipe (M/H 1.7 - L2301) Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	- 14	03-Jan-18	18-Jan-18														
SIV12155	Road kerb Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	- 10	01-Mar-18	12-Mar-18										 				
SIV12160	formation Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Black top	- 10	13-Mar-18	23-Mar-18														
SIV12165	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath -Utilities: HEC to MVB Plant room - cabling	21	02-Sep-17	26-Sep-17														
SIV12170	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Utilities: TCSS	22	27-Sep-17	23-Oct-17				: :						; ; !				
SIV12180	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - U channel	14	24-Oct-17	09-Nov-17														
SIV12220	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Paving block	45	10-Nov-17	04-Jan-18														
Section VII -	Remainder Works																	
Road & Drai	nage Works (Culvert L - M/H1.7, Adjacent to SR3)													; ; ! !				
SVII11600	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Drainage Works (Culvert L -MH1.7)	40	12-Dec-17	30-Jan-18														
SVII11640	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Gully pipe (Culvert L -MH1.7)	- 27	31-Jan-18	06-Mar-18														
SVII11650	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - TCSS duct , road kerb & formation	- 21	07-Mar-18	30-Mar-18										; ; ;				
SVII11660	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Black top	6	31-Mar-18	07-Apr-18														
SVII11680	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - U channel	14	07-Mar-18	22-Mar-18														
SVII11700	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - utilities	13	23-Mar-18	07-Apr-18														
SVII11720	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - paving block	11	09-Apr-18	24-Apr-18					1 1 1 1 1				1 1 1 1 1					
											<u> </u>							



CEDD Contract No. HK/2012/08 **Wan Chai Development Phase II** Central - Wan Chai Bypass at Wan Chai West

Page: 5 / 5

