CONTRACT NO: HK/2015/01

WANCHAI DEVELOPMENT PHASE II AND CENTRAL WANCHAI BYPASS SAMPLING, FIELD MEASUREMENT AND TESTING WORK (STAGE 3)

ENVIRONMENTAL PERMIT NO. EP-376/2009, FURTHER ENVIRONMENTAL PERMITS NO. FEP-01/376/2009 AND FEP-02/376/2009

MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT

- DECEMBER 2017 -

CLIENTS:

Civil Engineering and Development Department

PREPARED BY:

Lam Geotechnics Limited

11/F Centre Point 181-185 Gloucester Road, Wanchai, H.K.

Telephone: (852) 2882-3939 Facsimile: (852) 2882-3331 E-mail: info@lamenviro.com

Website: http://www.lamenviro.com

CERTIFIED BY:

Raymond Dai

Environmental Team Leader

DATE:

January 2018



Ref.: AACWBIECEM00 0 10078L.17

9 January 2018

By Post and Fax (2691 2649)

AECOM Asia Company Limited 11/F Tower 2 Grand Central Plaza 138 Shatin Rural Committee Road Shatin New Territories Hong Kong

Attention: Mr. Conrad Ng

Dear Mr. Ng,

Re: Contract No. HK/2015/01

Wan Chai Development Phase II - Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3)

Monthly Environmental Monitoring and Audit Report (December 2017) for EP-376/2009, FEP-01/376/2009 and FEP-02/376/2009

Reference is made to the Environmental Team's submission of the captioned Monthly Environmental Monitoring and Audit (EM&A) Report for December 2017 received by e-mail on 8 January 2018 for our review and comment.

Please be informed that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 in the captioned Environmental Permit.

Thank you very much for your attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,

David Yeung

Independent Environmental Checker

C.C.

CEDD

Attn: Mr. L K Tsang

by fax: 2577 5040

Lam

Attn: Mr. Raymond Dai

by fax: 2882 3331

AECOM

Attn: Mr. Francis Leong/ Stephen Lai by fax: 2691 2649

Q:\Projects\AACWBIECEM00\Corr\2017\AACWBIECEM00_0_10078L.17.docx



TABLE OF CONTENTS

EXE	CUTIVE	SUMMARY	3
1	INTR	ODUCTION	5
	1.1 1.2	Scope of the ReportStructure of the Report	
2	PROJ	ECT BACKGROUND	7
	2.1 2.2 2.3	Background Scope of the Project and Site Description Project Organization and Contact Personnel	7
3	STAT	US OF REGULATORY COMPLIANCE	10
	3.1	Status of Environmental Licensing and Permitting under the Project	10
4	MON	TORING REQUIREMENTS	12
	4.1 4.2	Noise MonitoringAir Quality Monitoring	
5	MON	TORING RESULTS	15
	5.1 5.2 5.3	Noise Monitoring Results Air Quality Monitoring Results Waste Monitoring Results	15
6	COM	PLIANCE AUDIT	18
	6.1 6.2 6.3 6.4	Noise Monitoring Air Quality Monitoring Review of the Reasons for and the Implications of Non-compliance Summary of action taken in the event of and follow-up on non-compliance	18 18
7	CUMI	JLATIVE CONSTRUCTION IMPACTS DUE TO THE CONCURRENT PROJECTS	19
8	ENVI	RONMENTAL SITE AUDIT	20
9	COM	PLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION	21
10	CON	CLUSION	22



LIST OF TABLES

<u>Table 2.1</u>	Schedule 2 Designated Projects under this Project
<u>Table 2.2</u>	Contact Details of Key Personnel
<u>Table 3.1</u>	Summary of the current status on licences and/or permits on environmental
	protection pertinent to the Project
<u>Table 3.2</u>	Cumulative Summary of Valid Licences and Permits under Contract no. HK/2012/08
Table 3.3	Summary of submission status under FEP-01/376/2009 Condition
Table 4.1	Noise Monitoring Stations
Table 4.2	Air Quality Monitoring Stations
Table 5.1	Noise Monitoring Stations for Contract no. HK/2012/08
Table 5.2	Air Quality Monitoring Station for Contract no. HK/2012/08
<u>Table 5.3</u>	Details of Waste Disposal for Contract no. HK/2012/08
<u>Table 8.1</u>	Summary of Environmental Inspections for Contract no. HK/2012/08
Table 9.1	Cumulative Statistics on Complaints
Table 9.2	Cumulative Statistics on Successful Prosecutions
<u>Table 10.1</u>	Summary of Key Construction Activities of Individual Contract(s) to be
	commenced in Coming Reporting Month

LIST OF FIGURES

Figure 2.1	Project Layout
Figure 2.2	Project Organization Chart
Figure 4.1	Locations of Environmental Monitoring Stations

LIST OF APPENDICES

Appendix 3.1	Environmental Mitigation Implementation Schedule
Appendix 4.1	Action and Limit Level
Appendix 4.2	Copies of Calibration Certificates
Appendix 5.1	Monitoring Schedule for Reporting Month and Coming month
Appendix 5.2	Noise Monitoring Results and Graphical Presentations
Appendix 5.3	Air Quality Monitoring Results and Graphical Presentations
Appendix 6.1	Event Action Plans
Appendix 6.2	Notification of Exceedance
Appendix 9.1	Complaint Log
Appendix 10.1	Construction Programme of Individual Contracts

Lam Geotechnics Limited

EXECUTIVE SUMMARY

- i. This is the Environmental Monitoring and Audit (EM&A) Monthly Report December 2017 specific for Environmental Permit no. EP-376/2009 and Further Environmental Permits no. FEP-01/376/2009 and FEP-02/376/2009. The EM&A report is prepared by the Environmental Team (ET) employed under Contract No. HK/2015/01 Wan Chai Development Phase II and Central Wanchai Bypass Sampling, Field Measurement and Testing Works (Stage 3). This report presents the environmental monitoring findings and information recorded during the period of 27th November 2017 to 26th December 2017. The cut-off date of reporting is at 26th of each reporting month.
- ii. In the reporting month, the principal work activities of the contract are included as follows:
 Contract no. HK/2012/08 Wan Chai Development Phase II Central- Wan Chai Bypass at Wan Chai West
 - Drainage
 - Roadworks

Noise Monitoring

- iii. Noise monitoring was conducted at M1a Harbour Road Sports Centre.
- iv. With respect to the shift in major construction site portions at Wan Chai North, the noise monitoring station M1a – Harbour Road Sports Centre was finely adjusted from East of Harbour Road Sports Centre to West of Harbour Road Sports Centre on 21 June 2016.
- v. With respect to the demolition of Ex-Harbour Road Sports Centre, the respective noise monitoring station M1a Harbour Road Sports Centre were finely adjusted on 16 and 25 May 2017 and thereafter to the Footbridge for Harbour Road Sports for noise monitoring.
- vi. Two action exceedances were recorded on 4 and 11 December 2017 in this reporting month.

 After the investigation, the exceedances were concluded as non-project related.

Air Quality Monitoring

- vii. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted on every six days basis at CMA5b Pedestrian Plaza and CMA6a Contractor HK/2012/08 Site Office.
- viii. One 24hr TSP action level exceedance and two 1hr TSP action level exceedance were recorded at CMA5b Pedestrian Plaza on 11, 12 and 23 December 2017 in the reporting month. After the investigation, the exceedances were concluded as non-Project related.

Complaints, Notifications of Summons and Successful Prosecutions

ix. No environmental complaint was received in this reporting month.



Lam Geotechnics Limited

Site Inspections and Audit

x. The Environmental Team (ET) conducted weekly site inspection for Contract no. HK/2012/08 in this reporting period. The Contractors rectified major observations and recommendations made during the audit sessions. No non-conformance was identified during the site inspections.

Future Key Issues

xi. In the coming reporting month, the principal work activities of the contract is anticipated as follows:

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West</u>

- Drainage
- Roadworks



1 INTRODUCTION

1.1 Scope of the Report

1.1.1. Lam Geotechnics Limited (LGL) has been appointed take up the role as the Environmental Team (ET) under Environmental Permit no. EP-376/2009 and Further Environmental Permits no. FEP-01/376/2009 and FEP-02/376/2009 to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Wan Chai Development Phase II and Central-Wan Chai Bypass (Register No.: AEIAR-458/2008).

This report documents the finding of EM&A works for Environmental Permit (EP) no. EP-376/2009 and Further Environmental Permits no. FEP-01/376/2009 and FEP-02/376/2009, during the period of 27th November 2017 to 26th December 2017. The cut-off date of reporting is the 26th of each reporting month.

1.2 Structure of the Report

Section 1 *Introduction* – details the scope and structure of the report.

Section 2 Project Background - summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.

Section 3 Status of Regulatory Compliance - summarizes the status of valid Environmental Permits / Licenses during the reporting period.

Section 4 *Monitoring Requirements* – summarizes all monitoring parameters, monitoring methodology and equipment, monitoring locations, monitoring frequency, criteria and respective event and action plan and monitoring programmes.

Section 5 Monitoring Results - summarizes the monitoring results obtained in the reporting period.

Section 6 Compliance Audit - summarizes the auditing of monitoring results, all exceedances environmental parameters.

Section 7 Cumulative Construction Impact due to the Concurrent Projects summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.



Section 8	Environmental Site Audit - summarizes the findings of weekly site
	inspections undertaken within the reporting period, with a review of any
	relevant follow-up actions within the reporting period.

Section 9 Complaints, Notification of summons and Prosecution – summarizes the cumulative statistics on complaints, notification of summons and prosecution

Section 10 Conclusion

2 PROJECT BACKGROUND

2.1 Background

2.1.1 Wan Chai Development phase II and Central-Wan Chai Bypass (hereafter called "the Project") are Designated Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Report for Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) has been approved on 11 December 2008.

2.2 Scope of the Project and Site Description

- 2.2.1. The design and construction of Wan Chai Development Phase II and Central Wanchai Bypass involves the construction and operation of primary and district distributor roads that is shown at *Figure 2.1*.
- 2.2.2. The key purpose of the study area encompasses the Wan Chai harbourfront area. The area starts at the boundary of Central Reclamation Phase III (CRIII) at the west and connects to the existing Hung Hing Road at the east. The scope of the project includes:
 - A dual 2-lane primary distributor road, Road P2, approximately 0.6km in length; and
 - Other new primary and district distributor roads connecting to the slip roads of the Central-Wan Chai Bypass with a total length of approximately 0.7km.
- 2.2.3. The project also contains various Schedule 2 DP that, under the EIAO, require Environmental Permits (EPs) to be granted by the DEP before they may be either constructed or operated.
 Table 2.1 summarises the DP under this Project. <u>Figure 2.1</u> shows the locations of these Schedule 2 DP.

Table 2.1 Schedule 2 Designated Project under this Project

Item	Designated Project	EIAO Reference	
DP2	Road P2 and other roads which are classified as	Schedule 2, Part I, A.1	
	primary/district distributor roads		

2.2.4. The designated project work II (DP2) was awarded to China State-Leader Joint Venture HK/2012/08 (Contract Title: Wan Chai Development Phase II Central – Wan Chai Bypass at Wan Chai West) as part of the Project works by the Civil Engineering and Development Department (CEDD). The construction work under Contract no. HK/2012/08 was commenced on 13 May 2015.



2.3 Project Organization and Contact Personnel

- 2.3.1 Civil Engineering and Development Department and Highway Department are the overall project controllers for the Wan Chai Development Phase II and Central-Wan Chai Bypass respectively. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.3.2 The proposed project organization and lines of communication with respect to environmental protection works are shown in *Figure 2.2*. Key personnel and contact particulars are summarized in *Table 2.2*:

Table 2.2 Contact Details of Key Personnel

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Principal Resident Engineer	Mr. Frankie Fan	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3922 3388	3912 3010
China State- Build King	Contractor under Contract	Project Director	C. N. LAI	9106 5806	2877 1522
Joint Venture	no. HK/2012/08	Site Agent	Mr. Keith Tse	9037 1839	
		Environmental Officer	Mr. James Ma	9130 9549	
		Environmental Supervisor	Mr. Y.L. Ho	9856 5669	
Ramboll Environ Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	3465 2888	3465 2899
Lam Geotechnics Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331



Contract No. HK/2015/01 Wan Chai Development Phase II and Central Wanchai Bypass - Sampling, Field Measurement and Testing Works (Stage 3) Monthly EM&A Report (December 2017)

- 2.3.3 In this reporting month, the principal work activities of the contract is included as follows:

 <u>Contract no. HK/2012/08 Wan Chai Development Phase II Central- Wan Chai Bypass at Wan Chai West</u>
 - Drainage
 - Roadworks
- 2.3.4 In coming reporting month, the principal work activities of the contract is anticipated as follows:

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West</u>

- Drainage
- Roadworks

3 STATUS OF REGULATORY COMPLIANCE

3.1 Status of Environmental Licensing and Permitting under the Project

3.1.1. A summary of the current status on licences and/or permits on environmental protection pertinent to the Project is shown in *Table 3.1*.

Table 3.1 Summary of the current status on licences and/or permits on environmental protection pertinent to the Project

Permits and/or Licences	Reference No.	Issued Date	Status
Environmental Permit	EP-376/2009	13 Nov 2009	Valid
Further Environmental Permit	FEP-01/376/2009	31 Mar 2015	Valid
Further Environmental Permit	FEP-02/376/2009	1 Aug 2016	Valid

3.1.2. The current status on licences and/or permits on environmental protection pertinent for contract no. HK/2012/08 under FEP-02/376/2009 showed in *Table 3.2*. and *Table 3.3*

Table 3.2 Cumulative Summary of Valid Licences and Permits under Contract no. HK/2012/08

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-01/376/2009	31 Mar 2015	N/A	Valid
Turtier Environmental Termit	FEP-02/376/2009	1 Aug 2016	N/A	Valid
Notification of Works Under APCO	355439	4 Feb 2013	N/A	Valid
Registration as a Chemical Waste Producer	5213-134-C3790-01	30 Jun 2016	N/A	Valid
Billing Account under Waste Disposal Ordinance	7016883	18 Feb 2013	N/A	Valid
Water Discharge Licence	WT00018470-2014	6 Mar 2014	31 Mar 2019	Valid
Construction Noise Permit	GW-RS0503-17	8 Jun 2017	13 Jul 2017 to 12 Jan 2018	Valid
Constitution Continu	GW-RS0914-17	23 Oct 2017	5 Nov 2017 to 4 Apr 2018	Valid

1,



Lam Geotechnics Limited

Table 3.3 Summary of submission status under FEP-01/376/2009 Condition

EP Condition	Submission	Date of Submission
Condition 2.9	Noise Management Plan (Rev. 2)	Generally in order as commented by EPD on 27 Oct 2015
Condition 2.10	Landscape Plan (Rev. 0)	Generally in order as commented by EPD on 5 Aug 2015

3.1.3. Implementation status of the recommended mitigation measures during this reporting month is presented in *Appendix 3.1*.



4 MONITORING REQUIREMENTS

4.1 Noise Monitoring

NOISE MONITORING STATION

4.1.1. The noise monitoring station for the Project is listed and shown in *Table 4.1* and *Figure 4.1*.
Appendix 4.1 shows the established Action/Limit Levels for the monitoring works.

Table 4.1 Noise Monitoring Station

District	Station	Description
Wan Chai	M1a	Footbridge for Ex-Harbour Road Sports Centre

NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.1.2. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (Leq). Leq (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods, Leq (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. Supplementary information for data auditing, statistical results such as L10 and L90 shall also be obtained for reference.
- 4.1.3. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
 - One set of measurements between 0700 and 1900 hours on normal weekdays.

MONITORING EQUIPMENT

- 4.1.4. As referred to in the Technical Memorandum ™ issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.
- 4.1.5. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

4.2 Air Quality Monitoring

AIR QUALITY MONITORING STATIONS

4.2.1. The air quality monitoring stations for the Project are listed and shown in *Table 4.2* and *Figure*4.1. Appendix 4.1 shows the established Action/Limit Levels for the monitoring works.

Table 4.2 Air Quality Monitoring Stations


Station ID	Description
CMA5b	Pedestrian Plaza
CMA6a	WDII PRE Site Office

AIR QUALITY MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 4.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.
- 4.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.

SAMPLING PROCEDURE AND MONITORING EQUIPMENT

- 4.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:
 - 0.6 1.7 m³ per minute adjustable flow range;
 - Equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
 - Installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
 - Capable of providing a minimum exposed area of 406 cm2;
 - Flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
 - Equipped with a shelter to protect the filter and sampler;
 - Incorporated with an electronic mass flow rate controller or other equivalent devices;
 - Equipped with a flow recorder for continuous monitoring;





- Provided with a peaked roof inlet;
- Incorporated with a manometer;
- Able to hold and seal the filter paper to the sampler housing at horizontal position;
- · Easily changeable filter; and
- Capable of operating continuously for a 24-hour period.
- 4.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

LABORATORY MEASUREMENT / ANALYSIS

- 4.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.
- 4.2.8. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.
- 4.2.9. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.
- 4.2.10. All the collected samples shall be kept in a good condition for 6 months before disposal.
- 4.2.11. Current calibration certificates of equipment are presented in *Appendix 4.2*.

5 MONITORING RESULTS

- 5.0.1. The environmental monitoring will be implemented based on the division of works areas of the designated project managed under the contract with FEP applied by individual contractors. Overall layout showing work areas of various contracts, latest status of work commencement and monitoring stations is shown in Figure 2.1 and Figure 4.1. The monitoring results are presented in according to the Individual Contract(s).
- 5.0.2. In the reporting month, the concurrent contract is:
 - Contract no. HK/2012/08 Wan Chai Development Phase II Central Wan Chai Bypass at Wan Chai West.
- 5.0.3. The environment monitoring schedules for reporting month and coming month are presented in *Appendix 5.1*.

5.1 Noise Monitoring Results

5.1.1 The proposed division of noise monitoring station is summarized in *Table 5.1* below.

Table 5.1 Noise Monitoring Station for Contract no. HK/2012/08

Location ID	District	Description
M1a	Wan Chai	Footbridge for Ex-Harbour Road Sports Centre

- 5.1.2 Two action level exceedances were recorded on 4 and 11 December 2017 in this reporting month.
- 5.1.3 After the investigation, no construction work under EP-376/2009 was conducted by Contract HK/2012/08 on 4 December 2017 around the concerned location during the time of measurement while non WDII-CWB excavation works immediately next to the monitoring station was observed as the major noise contribution during monitoring. As such, the exceedance was considered as not related to Project works under Contract HK/2012/08.
- 5.1.4 After the investigation, no construction work under EP-376/2009 was conducted by Contract HK/2012/08 on 11 December 2017 around the concerned location during the time of measurement while non WDII-CWB breaking works next to the monitoring station was observed as the major noise contribution during monitoring. As such, the exceedance was considered as not relate to Project works under HK/2012/08.
- 5.1.5 The noise monitoring results measured in this reporting period are reviewed and summarized.
 Details of the noise monitoring results and graphical presentation can be referred to <u>Appendix</u>
 5.2.



5.2 Air Quality Monitoring Results

5.2.1 The proposed division of air quality monitoring stations are summarized in *Table 5.2* below.

Table 5.2 Air Quality Monitoring Station for Contract no. HK/2012/08

Station	Description
CMA5b	Pedestrian Plaza
CMA6a	WDII PRE Site Office

- 5.2.2 One 24hr TSP action level exceedance and one 1hr TSP action level exceedance were recorded at CMA5b - Pedestrian Plaza on 11 and 12 December 2017. Road and drains works for P2 road was undertaken by the Contractor of HK/2012/08 around the monitoring location on the monitoring date and no particular observation regarding air quality impact was observed during sampling. Meanwhile, non WDII-CWB Project construction activities was observed opposite to the monitoring station on the monitoring date. According to the EPD monitoring record, AQHI recorded at the Causeway Bay station was recorded as Lv4 - Lv7 on 11 December 2017 and recorded as Lv6 on 12 December 2017 during the monitoring period indicating the adverse ambient condition. In addition, similar elevation in TSP level were recorded across the same period on 11 December 2017 at other Project AQM stations including CMA6a at Wan Chai and CMA3a at Causeway Bay area suggesting overall air quality within the district was under influence of ambient pollutant. In view of the above, the exceedance was considered to be not related to the Project works under Contract HK/2012/08 and potentially contributed by ambient air quality condition. Nevertheless, the Contractor of HK/2012/08 was advised to strengthen the overall dust suppression control measures to ensure all dusty surface are dampened to avoid potential dust emission.
- 5.2.3 One 1hr TSP action level exceedances was recorded at CMA5b Pedestrian Plaza on 23 December 2017. Road and drains works for P2 road was undertaken by the Contractor of HK/2012/08 around the monitoring location on the monitoring date and no particular observation regarding air quality impact was observed during sampling. Meanwhile, non WDII-CWB Project excavation material handling was observed opposite to the monitoring station on the monitoring date. In addition, elevated PM2.5 and PM10 level were recorded at the EPD Causeway Bay monitoring station across the monitoring period suggesting the meteorological condition at the time of monitoring may not favor the dispersion of ambient air pollutant within the district and hence affecting the air quality. In view of the above, the exceedance was considered to be not related to the Project works under Contract HK/2012/08 and potentially contributed by ambient air quality condition. Nevertheless, the Contractor of HK/2012/08 was advised to strengthen the overall dust suppression control measures to ensure all dusty surface are dampened to avoid potential dust emission.
- 5.2.4 The air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in *Appendix* 5.3.

5.3 WASTE MONITORING RESULTS

5.3.1 No Inert and non-inert C&D wastes disposed in this reporting month. Details of the waste flow table are summarized in *Table 5.3*.

Table 5.3 Details of Waste Disposal for Contract no. HK/2012/08

Waste Type	Quantity this month	Cumulative Quantity- to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m3	NIL	NIL	NIL
Inert C&D materials recycled, m3	NIL	NIL	NIL
Non-inert C&D materials disposed, m3	NIL	NIL	NIL
Non-inert C&D materials recycled, m3	NIL	NIL	NIL
Chemical waste disposed, kg	NIL	NIL	NIL



Lam Geotechnics Limited

6 COMPLIANCE AUDIT

6.0.1. The Event Action Plan for construction noise and air quality are presented in Appendix 6.1.

6.1 Noise Monitoring

6.1.1 Two action level exceedances were recorded on 4 and 11 December 2017 in this reporting month. After the investigation, the exceedances were concluded as non-project related.

6.2 Air Quality Monitoring

6.2.1 One 24hr TSP action level exceedance and two 1hr TSP action level exceedance were recorded at CMA5b – Pedestrian Plaza on 11, 12 and 23 December 2017 in the reporting month. After the investigation, the exceedances were concluded as non-Project related.

6.3 Review of the Reasons for and the Implications of Non-compliance

6.3.1 There was no non-compliance from the site audits in the reporting period. The observations and recommendations made in each individual site audit session were presented in Section 8.

6.4 Summary of action taken in the event of and follow-up on non-compliance

6.4.1 There was no particular action taken since no non-compliance was recorded from the site audits in the reporting period.



7 CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS

- 7.0.1. According to the Condition 3.4 of the EP-376/2009, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) and Wan Chai Development Phase II Central Wan Chai Bypass at Wan Chai East (CWB Tunnel).
- 7.0.2. According to the Final EM&A report of Central Reclamation Phase III (CRIII) for Contract HK 12/02, the major construction activities were completed by end of January 2014 and no construction activities were undertaken thereafter and the water quality monitoring was completed in October 2011. As such, it is considered that there were no cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) undertaken by contractor HK12/02 in the reporting month.
- 7.0.3. According to the construction programme of Central-Wanchai Bypass at Wanchai West at the Central Reclamation Phase III area include roadworks, back-filling, reinstatement of culvert K, reinstatement of cooling mains, drainage, trimming of rock level and reinstatement of the planter after installation of irrigation pipes and waterworks at P1 Road were performed in December 2017 reporting period. As no project related exceedance were recorded during the reporting period, cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was considered as insignificant.
- 7.0.4. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activities under Wan Chai Development Phase II were road and drains construction and backfilling works at Wan Chai West and Wan Chai East. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were drainage works and ventilation building construction at Central; temporary reclamation removal works at Causeway Bay, road works at Victoria Park; bridge construction, approach ramp construction and building construction at North Point area in the reporting period. In addition, other non-Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects was observed undertaken at Wan Chai North and North Point area.
- 7.0.5. No significant air impact from construction activities was anticipated in the reporting month. Besides, no project related exceedance was recorded during the water, air and noise environmental monitoring events in the reporting month. Thus, it is evaluated that the cumulative construction impact from the concurrent projects including Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) was insignificant.



Lam Geotechnics Limited

8 ENVIRONMENTAL SITE AUDIT

8.0.1. Four site inspections for Contract no. HK/2012/08 were carried out on 28 November, 5, 12 and 19 December 2017 in this reporting period. The results of inspection and outcome are summarized in *Table 8.1.*

Table 8.1 Summary of Environmental Inspections for Contract no. HK/2012/08

Item	Date	Observations	Action taken by Contractor	Outcome
171205_01	5-Dec-17	Watering shall be provided to idle stockpile (Zone B)	The concerned stockpile was removed	Completion as observed on 12 December 2017
171212_01	12-Dec-17	Watering shall be provided to dusty surface to avoid dust emission (Zone C-W & C-E)	Watering was provided to dusty surface	Completion as observed on 19 December 2017
171212_02	12-Dec-17	Wheel washing at site exit shall be enhance (Slip Road 1 Zone D)	Cleaning of site exit was provided at Slip Road 1 Zone D	Completion as observed on 19 December 2017

Lam Geotechnics Limited

COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION 9

- No environmental complaint was received in the reporting period.
- 9.0.2. The details of cumulative complaint log and updated summary of complaints are presented in Appendix 9.1
- 9.0.3. Cumulative statistic on complaints and successful prosecutions are summarized in Table 9.1 and Table 9.2 respectively.

Table 9.1 Cumulative Statistics on Complaints

Reporting Period	No. of Complaints
Commencement works (May 2015) to last reporting month	0
December 2017	0
Total	0

Table 9.2 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative No. Project-to-Date
Air	0	0	0
Noise	0	0	0
Water	0	0	0
Waste	0	0	0
Total	0	0	0

10 CONCLUSION


- 10.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.
- 10.0.2. The scheduled construction activities and the recommended mitigation measures for the coming month are listed in *Table 10.1*. The construction programmes of individual contracts are provided in *Appendix 10.1*.

Table 10.1 Summary of Key Construction Activities of Individual Contract(s) to be commenced in Coming Reporting Month

Contract No.	Key Construction Works	Recommended Mitigation Measures
HK/2012/08	Drainage Deadwarks	Dust control during dust generating works:
	Roadworks	Implementation of proper noise pollution control; and
		Provision of protection to ensure no runoff out of site area or direct discharge into public drainage system

Figure 2.1

Project Layout

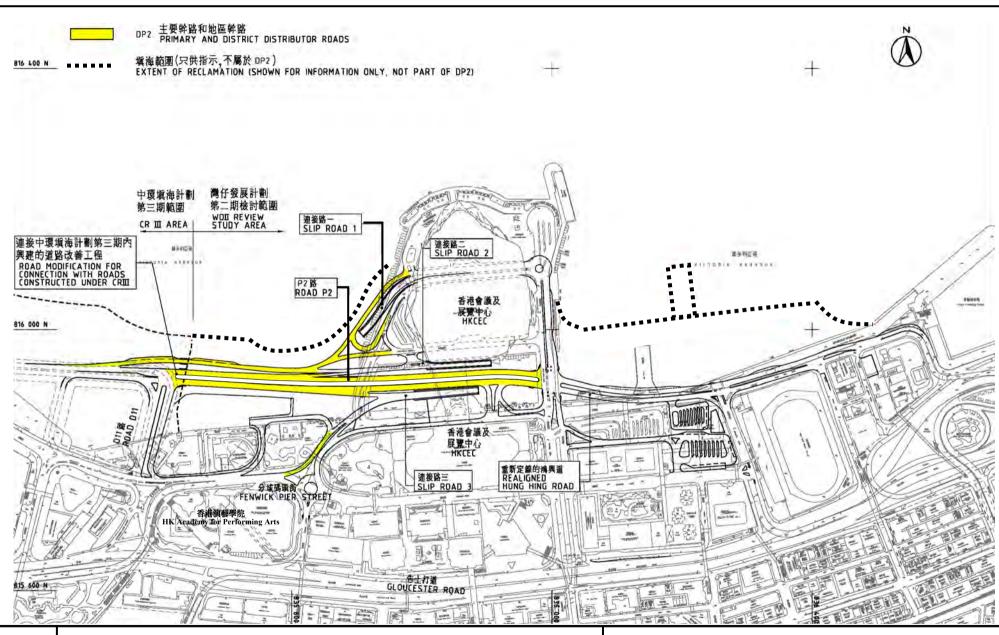



Project Title : Road P2 and other roads which are classified as primary/district distributor roads (referred to as "DP2" in the WDII&CWB EIA Report)

工程項目名稱: P2 路及其他分類爲主要幹路或地區幹路的道路(WDII&CWB 環評報告內稱 "DP2")

Environmental Permit No.: EP-376/2009 環境許可證編號 : EP-376/2009 Figure 1: Location of the Project

圖 1: 工程項目位置圖

(This figure was prepared based on Figure 1.2b of the WDII&CWB EIA report (Register No.: AEIAR-125/2008)) (本圖是根據 WDII&CWB 環評報告(登記冊編號 AEIAR-125/2008)圖 1.2b 編制)

Figure 2.2

Project Organization Chart

Project Organization Chart


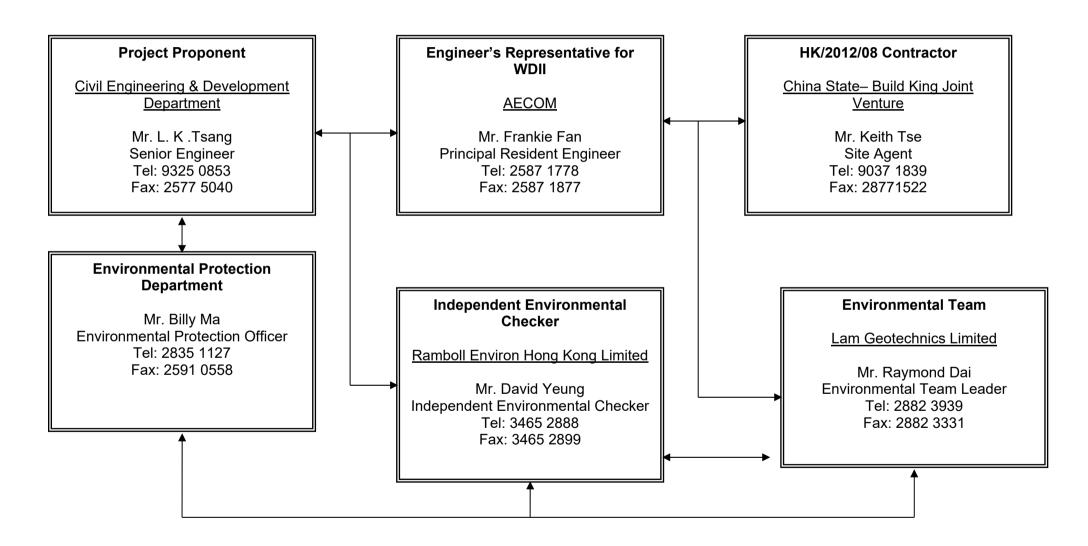


Figure 4.1

Locations of Monitoring Stations

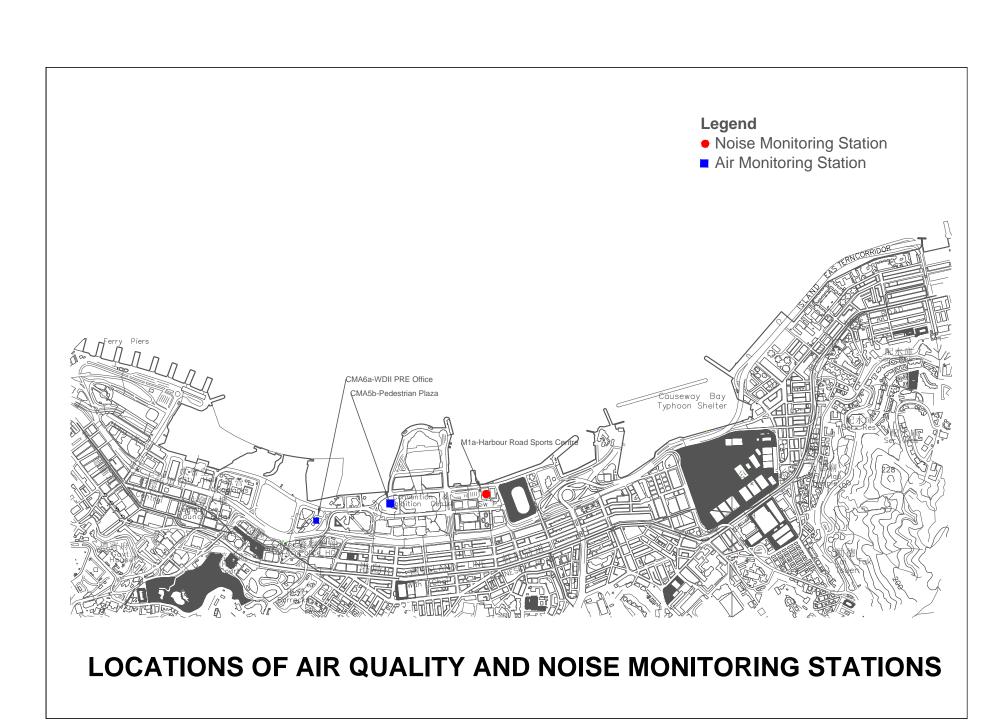

Appendix 3.1

Environmental Mitigation Implementation Schedule

Appendix A

Table A13.1 Implementation Schedule for Air Quality Control

Table A13.2 Implementation Schedule for Noise Control

Table A13.3 Implementation Schedule for Water Quality Control

Table A13.4 Implementation Schedule for Waste Management

Table A13.7 Implementation Schedule for Landscape and Visual

IMPLEMENTATION SCHEDULE OF THE PROPOSED MITIGATION MEASURES

Table A13.1 Implementation Schedule for Air Quality Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Impl	ement	ation	stage	Relevant Legislation
				Des	C	О	Dec	and Guidelines
Constructio	n Phase							
For the Who	ole Project							
S3.6.5	Four times a day watering of the work site with active operations.	Work site / during construction	Contractor		1			EIAO-TM
S3.8.1	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimise cumulative dust impacts. Strictly limit the truck speed on site to below 10 km per hour and water spraying to keep the haul roads in wet condition; Watering during excavation and material handling; Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary; and Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.	Work site / during construction	Contractor		V			

Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Table A13.2 Implementation Schedule for Noise Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Impl	lemen	tation :	stage	Relevant Legislation and Guidelines
				Des	C	О	Dec	
Constructio	n Phase		L					
For the Who	ole Project							
S4.9.4	Good Site Practice: Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program. Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program. Mobile plant, if any, shall be sited as far away from NSRs as possible. Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum. Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from onsite construction activities.	Work site / during construction	Contractor		V			EIAO-TM, NCO
S4.8.3 – S4.8.4	Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the	Work site / during construction	Contractor		V			EIAO-TM, NCO
	following tasks: Temporary road diversion Resurfacing At-grade roadwork							

[•] Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

Table A13.3 Implementation Schedule for Water Quality Control

	installed in order to minimise the sediment loading of the effluent prior to discharge; All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge shall be adequately designed for the controlled release of storm flows. All sediment control measures shall be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage shall be reinstated to its original condition when the construction work is finished or the temporary diversion is no longer required. All fuel tanks and store areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity. Minimum distances of 100 m shall be maintained between the storm water discharges				
S5.8	and the existing or planned WSD flushing water intakes during construction phase. Sewage from Construction Work Force Construction work force sewage discharges on site shall be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage shall be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor shall also be responsible for waste disposal and maintenance practices.	Work site / during construction	Contractor	N	ProPECC PN 1/94; WPCO (TM-DSS)

<u>EP-376/2009</u> EM&A Manual

S5.8	Floating Debris and Refuse	Work site and	Contractor			WPCO
	Collection and removal of floating refuse shall	adjacent water /				
	be performed at regular intervals on a daily	During the				
	basis. The contractor shall be responsible for	construction period.				
	keeping the water within the site boundary and					
	the neighbouring water free from rubbish.					
S5.8	Storm Water Discharges	Work site and	Contractor	 		WPCO
	Minimum distances of 100 m shall be	adjacent water				
	maintained between the existing or planned	/ During the design				
	stormwater discharges and the existing or	and construction				
	planned WSD flushing water intakes.	period.				

• Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

Table A13.4 Implementation Schedule for Waste Management

EIA Ref	Environmental Protection Measures /	Location / Timing	Implementation	Imp	lemen	tation	stage	Relevant Legislation
	Mitigation Measures		Agent	Des	C	О	Dec	and Guidelines
Construction	on Phase		<u>l</u>	1				<u> </u>
For the Who	ole Project							
S6.7.7	Good Site Practices Recommendations for good site practices during the construction activities include: nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; training of site personnel in proper waste management and chemical waste handling procedures; provision of sufficient waste disposal points and regular collection for disposal; appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and a recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).	Work site / During planning and design stage, and construction stage	Contractor					
S.6.7.8	Waste Reduction Measures Recommendations to achieve waste reduction include: • Sort C&D waste from demolition of the existing waterfront structures to recover	Work site / During planning and design stage, and construction stage	Contractor	V	V			

	 recyclable portions such as metals. Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal. Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force. Any unused chemicals or those with remaining functional capacity shall be recycled. Use of reusable non-timber formwork, such as in casting the tunnel box sections, to reduce the amount of C&D material. Proper storage and site practices to minimise the potential for damage or contamination of construction materials. Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. 				
S6.7.10	General Refuse General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D material.	Work site / During the construction period	Contractor	V	Public Health and Municipal Services Ordinance (Cap. 132)
	A collection area shall be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind blow' light material.				

S6.7.11	Chemical Wastes After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals shall be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work site / During the construction period	Contractor	V	Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
S6.7.12 – S6.7.13	Construction and Demolition Material C&D material shall be sorted on-site into inert C&D material (that is, public fill) and C&D waste. All the suitable inert C&D material shall be broken down to 250 mm in size for reuse as public fill in the WDII reclamation. C&D waste, such as wood, glass, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials.	Work site / During the construction period	Contractor and Independent Environmental Checker	V	DEVB TCW No.6/2010; ETWB TCW No. 33/2002; ETWB TCW No. 19/2005
	In order to monitor the disposal of public fill and C&D waste at public fill reception facilities and landfills, respectively, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team undertaking the environmental monitoring and audit work. An Independent Environment Checker shall be responsible for auditing the results of the system.				
S6.7.14	Bentonite Slurry The disposal of residual used bentonite slurry shall follow the good practice guidelines stated	Work site / During the construction period	Contractor	V	ProPECC PN 1/94

EP-376/2009 EM&A Manual in ProPECC PN 1/94 "Construction Site Drainage" and listed as follows: If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis. If the used bentonite slurry is intended to be disposed of through the public drainage system, it shall be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the Technical Memorandum of Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters. If the used bentonite slurry is intended to be disposed to public fill reception facilities, it will be mixed with dry soil on site before disposal.

• Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

Table A13.7 Implementation Schedule for Landscape and Visual

EIA Ref	Environmental Protection Measures /	Location / Timing	Implementation	Implementation stage				Relevant Legislation
	Mitigation Measures		Agent	Des	C	0	Dec	and Guidelines
Construction	n Phase		1		1			
For the Who	le Project							
Table 10.5	CM1 Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	V	1			EIAO TM
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	1	1			EIAO TM
Table 10.5	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	1	1			EIAO TM
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		1			EIAO TM
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		1			EIAO TM
For DP2 - V	VDII Major Roads (Road P2)							
Table 10.5	CM1 Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	√	1			EIAO TM
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	1	√			EIAO TM
Table 10.5	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	1	√			EIAO TM
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		1			EIAO TM

Operation Pl	nase					
•	DII Major Roads (Road P2)					
Table 10.6, Figure	OM1 Aesthetic design of buildings and road- related structures,	Work site / During Design Stage and	CEDD/HyD	V	1	ETWB TCW 2/2004
10.5.1-	including viaducts, vent buildings, subways,	Operation Phases				
10.5.5	footbridges					
Table 10.6,	and noise barriers and enclosure. OM3 Buffer Tree and Shrub Planting to screen	Work site / During	CEDD/HyD	V	1	ETWB TCW 2/2004
Figure	proposed roads	Design Stage and		'	'	
10.5.1-	and associated structures.	Operation Phases				
10.5.5 Table 10.6.	OM5 Aesthetic streetscape design.	Work site / During	CEDD/HyD	V	1	ETWB TCW 2/2004
Figure		Design Stage and			'	
10.5.1- 10.5.5		Operation Phases				
Table 10.6,	OM6 Aesthetic design of roadside amenity areas	Work site / During	CEDD/HyD	V	1	ETWB TCW 2/2004
Figure	22.20 22.20.000	Design Stage and			'	
10.5.1-		Operation Phases				
10.5.5						

[•] Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

Appendix 4.1

Action and Limit Level

Action and Limit Level

Action and Limit Level for Noise Monitoring

Time Period	Action Level	Limit Level
07:00 - 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A)

Notes: If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed. *The Limit level shall be 70 dB(A) and 65 dB(A) for educational institute during normal teaching periods and school examination periods, respectively.

Action and Limit Level for Air Monitoring

Monitoring Locations	1-hour TSP Le	1-hour TSP Level inµg/m3 2		evel inµg/m3
	Action Level Limit Level A		Action Level	Limit Level
CMA5b Pedestrian Plaza	339.7	500	209.9	260
CMA6a WDII PRE Site Office	333.0	500	207.1	260

Appendix 4.2

Copies of Calibration Certificates



TISCH ENVIRONMENTAL, INC. 145 SOUTH MIAMI AVE VILLAGE OF CLEVES, OH 45002 513.467.9000 877.263.7610 TOLL FREE 513.467.9009 FAX

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Ma Operator		Rootsmeter Orifice I.I		438320 0005	Ta (K) - Pa (mm) -	293 759.46
PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1 2 3 4 5	NA NA NA NA	NA NA NA NA	1.00 1.00 1.00 1.00	1.3960 0.9970 0.8910 0.8500 0.6990	3.2 6.4 7.8 8.7 12.7	2.00 4.00 5.00 5.50 8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
1.0120 1.0078 1.0058 1.0047 0.9993	0.7249 1.0108 1.1288 1.1820 1.4296	1.4257 2.0163 2.2543 2.3643 2.8514	0.9958 0.9916 0.9896 0.9885 0.9832	0.7133 0.9946 1.1107 1.1630 1.4066	0.8784 1.2423 1.3889 1.4567 1.7568
Ostd slop intercept coefficie y axis =	(b) = ent (r) =	2.02533 -0.03593 0.99983	 Qa slope intercept coefficie	t (b) =	1.26823 -0.02214 0.99983

CALCULATIONS

Vstd = Diff. Vol[(Pa-Diff. Hg)/760](298/Ta)

Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]

Qa = Va/Time

For subsequent flow rate calculations:

Qstd = $1/m\{[SQRT(H2O(Pa/760)(298/Ta))] - b\}$

 $Qa = 1/m\{[\dot{S}QRT \ H2O(Ta/Pa)] - b\}$



Calibration Data for High Volume Sampler (TSP Sampler)

Location	:	CMA5b	Calibration Date	:	20-Nov-17
Equipment no.	:]	HVS010	Calibration Due Date	: [20-Jan-18

CALIBRATION OF CONTINUOUS FLOW RECORDER

	Ambient Condition								
Temperature, T _a	292	Kelvin	Pressure, P _a	1019	mmHg				

Orifice Transfer Standard Information							
Equipment No.	Ori001	Slope, m _c	2.02533	Intercept, bc	-0.03593		
Last Calibration Date	20-Mar-17	$(HxP_a/1013.3 \times 298/T_a)^{1/2}$					
Next Calibration Date	20-Mar-18		= <i>m</i>	$b_c \times Q_{std} + b_c$			

Calibration of TSP								
Calibration	Mai	nometer Re	eading	Q _{std}	Continuous Flow	IC		
Point	н	inches of v	water)	(m ³ / min.)	Recorder, W	(W(P _a /1013.3x298/T _a) ^{1/2} /35.31)		
	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis		
1	1.3	1.3	2.6	0.8243	40	40.5224		
2	2.2	2.2	4.4	1.0670	46	46.6007		
3	3.3	3.3	6.6	1.3028	52	52.6791		
4	4.4	4.4	8.8	1.5016	59	59.7705		
5	5.5	5.5	11.0	1.6767	62	62.8097		
By Linear Regression of Y	n X							
	Slope, m	=	27.0	0050 In	tercept, b = 18.	0599		
Correlation C	oefficient*	=	0.9	969				
Calibration	Accepted	=	Yes	Ne**				

^{*} if Correlation Coefficient < 0.990, check and recalibration again.

**	Delete	as	appropriate.
----	--------	----	--------------

Remarks: As per client's provided information, the equipment reference no. of the calibrated High Volume Sampler has been

re-assigned from EL222 to HVS010 with respect to the update in quality management system.

 Calibrated by
 :
 Jackey MA
 Checked by
 :
 Pauline Wong

 Date
 :
 20-Nov-17
 Date
 :
 20-Nov-17



Calibration Data for High Volume Sampler (TSP Sampler)

Location	:	CMA6a	Calibration Date	: _	20-Nov-17
Equipment no.	:	HVS013	Calibration Due Date	:	20-Jan-18

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition						
Temperature, T _a	292	Kelvin Pressure , P _a	1019	mmHg		

Orifice Transfer Standard Information							
Equipment No.	Ori001	Slope, m _c	2.02533	Intercept, bc	-0.03593		
Last Calibration Date	20-Mar-17		$(HxP_a/$	1013.3 x 298 / T _a)	1/2		
Next Calibration Date	20-May-17		= <i>m</i>	$_{c}$ \times Q_{std} + b_{c}			

	Calibration of TSP								
Calibration	Mai	nometer Re	eading	Q _{std}	Continuous Flow	IC			
Point	H (inches of water)		(m ³ / min.)	Recorder, W	(W(P _a /1013.3x298/T _a) ^{1/2} /35.31)				
	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis			
1	1.4	1.4	2.8	0.8547	34	34.4440			
2	2.3	2.3	4.6	1.0905	41	41.5354			
3	3.5	3.5	7.0	1.3411	48	48.6268			
4	4.5	4.5	9.0	1.5183	54	54.7052			
5	5.6	5.6	11.2	1.6917	58	58.7574			

Rν	Linear	Regression	οf	Υ	on X	
υy	Lilicai	regression	OI.			

Slope, m = 29.4252 Intercept, b = 9.3820

Correlation Coefficient* = 0.9992

Calibration Accepted = Yes/Ne**

Remarks: As per client's provided information, the equipment reference no. of the calibrated High Volume Sampler has been

re-assigned from EL551 to HVS013 with respect to the update in quality management system.

 Calibrated by Date
 : Jackey MA
 Checked by Date
 : Pauline Wong

 Date
 : 20-Nov-17
 Date
 : 20-Nov-17

^{*} if Correlation Coefficient < 0.990, check and recalibration again.

^{**} Delete as appropriate.



港 黄 竹 坑 道 3 7 號 利 達 中 心 1 2 樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Certificate No.:

17CA0426 01-02

Page

of

2

Item tested

Description:

Sound Level Meter (Type 1)

Microphone

Manufacturer: Type/Model No.:

Larson Davis LxT1

PCB

Serial/Equipment No.:

0003737

377B02 171529

Adaptors used:

Item submitted by

Customer Name:

Lam Environmental Service Ltd.

Address of Customer: Request No .: Date of receipt:

Date of test:

28-Apr-2017

26-Apr-2017

Reference equipment used in the calibration

Description:

Multi function sound calibrator

Model:

Serial No. 2288444

Expiry Date:

Traceable to:

Signal generator

B&K 4226 DS 360

61227

18-Jun-2017 01-Apr-2018 CIGISMEC CEPREI

Ambient conditions

Temperature:

21 ± 1 °C

Relative humidity: Air pressure:

50 ± 10 % 1010 ± 5 hPa

Test specifications

1. The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580; Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.

2, The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of +20%.

The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Min/Feng Jun Qi

Actual Measurement data are documented on worksheets.

Huano-dia

Approved Signatory:

Date:

04-May-2017

Company Chop:

The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

C Sals & Materials Engineering Co. Ltd.

Form No CARP152-1/Issue 1/Rev C/01/02/2007



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

17CA0426 01-02

Page

2

1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	
PRODUCTION STREET, SAME CONTRACTOR	C	Pass	0.8	2.1
	Lin	Pass	1.6	2.2
Linearity range for Leq	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
80 SEE 14	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	Α	Pass	0.3	
	A C	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	N/A	N/A	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/103 at 4kHz	Pass	0.3	
50.20	1 ms burst duty factor 1/10 ⁴ at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leg	Pass	0.4	

2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
	Weighting A at 8000 Hz	Pass	0.5	

Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

Lai Sheng Jie

Checked by:

e: 04

Date:

28-Apr-2017

Date:

Fung Chi Yip 04-May-2017

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

End

© Soils & Materials Engineering Co., Ltd.

Form No CARP152-2/Issue 1/Rev C/01/02/2007



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Certificate No.:

17CA1110 02

Page:

of

Item tested

Description: Manufacturer: Acoustical Calibrator (Class 1)

Type/Model No.

Rion Co., Ltd. NC-73

Serial/Equipment No.: Adaptors used:

10707358

Item submitted by

Curstomer

Lam Geotechnics Ltd.

Address of Customer:

Request No.: Date of receipt:

-10-Nov-2017

Date of test:

14-Nov-2017

Reference equipment used in the calibration

Signal generator DS 360 61227 01-Apr-2018 Digital multi-meter 34401A US36087050 25-Apr-2018 Audio analyzer 8903B GB41300350 21-Apr-2018 Universal counter 53132A MY40003662 23-Apr-2018	ligital multi-meter udio analyzer	34401A 8903B	US36087050	01-Apr-2018 25-Apr-2018	Traceable to: SCL CEPREI CEPREI CEPREI CEPREI CEPREI
---	--------------------------------------	-----------------	------------	----------------------------	--

Ambient conditions

Temperature:

21 ± 1 °C

Relative humidity:

50 ± 10 %

Air pressure:

1010 ± 5 hPa

Test specifications

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference
 pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure
 changes.

Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942; 1997 for the conditions under which the fest was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.

M/Feng Jun Qr

Huang Ji

Approved Signatory:

Date:

15-Nov-2017

Company Chop:

Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

© Soils & Materials Engineering Co. Ltd.

Form No. CARP156-1/Issue 1/Rev D/01/03/2007



香港黄竹坑遊37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

17CA1110 02

Page:

2

1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

(Output level in dB re 20 jsPa) Output Sound Pressure Measured Output Frequency Estimated Expanded Shown Level Setting Sound Pressure Level Uncertainty Hz d8 dB dB 1000 94.00 93 93 0.10

2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz

STF = 0.008 dB

Estimated expanded uncertainty

0.005 dB

3. Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz

Actual Frequency = 991.5 Hz

Estimated expanded uncertainty

0.1 Hz

Coverage factor k = 2.2

4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz

TND = 0.3 %

Estimated expanded uncertainty

0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

- End

Checked by:

Fung Chi Yip 15-Nov-2017

Date:

14-Nov-2017

calibrated on a schedule to maintain the required accuracy level.

Date:

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are

© Soils & Materials Engineering Co., Ltd.

Form Na CARP156-2/Issue 1/Rev C/01/05/200



香港 黄 竹 坑 雄 3 7 號 利 建 中 心 | 2 樓 12F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong, E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Certificate No.:

17CA1020 02

Page:

of

2

Item tested

Description:

Acoustical Calibrator (Class 1)

Manufacturer: Type/Model No.: Larson Davis CAL200

Scrial/Equipment No.: Adaptors used:

13437

Item submitted by

Curstomer:

Lam Geotechnics Ltd.

Address of Customer:

Request No.:

.

Date of receipt:

20-Oct-2017

Date of test:

23-Oct-2017

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2341427	11-Apr-2018	SCL
Preamplifier	B&K 2673	2239857	05-May-2018	CEPREI
Measuring amplifier	B&K 2610	2346941	03-May-2018	CEPREL
Signal generator	DS 360	61227	01-Apr-2018	CEPREI
Digital multi-meter	34401A	US36087050	25-Apr-2018	CEPREI
Audio analyzer	8903B	GB41300350	21-Apr-2018	CEPREI
Universal counter	53132A	MY40003662	22-Apr-2018	CEPREI
				Control of County

Ambient conditions

Temperature:

22 ± 1 °C 50 ± 10 %

Relative humidity: Air pressure:

1000 ± 5 hPa

Test specifications

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B
 and the lab calibration procedure SMTP004-CA-156.
- 2. The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference
 pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure
 changes.

Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator moots IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.

Min/Feng Jun Qi

Approved Signatory:

Date:

24-Oct-2017

Company Chop:

有限公司等

Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

© Soits & Materials Engineering Co., Ltd.

Form No CARP156-1/98be 1/Rev D/01/93/2007



香港黃竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

17CA1020 02

Page:

2

2

1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

Frequency Shown Hz	Output Sound Pressure Level Setting dB	Measured Output Sound Pressure Level d8	(Output level in dB re 20 µPa) Estimated Expanded Uncertainty dB
1000	94.0	93.90	0.10

2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz

STF = 0.011 dB

Estimated expanded uncertainty

0.005 dB

3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz

Actual Frequency = 1000.2 Hz

Estimated expanded uncertainty

0.1 Hz

Coverage factor k = 2.2

4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz

TND = 0.6 %

Estimated expanded uncertainty

0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

End

Checked by:

Date:

Chai Shilyng Jie 23-Oct-2017

Date:

Fung Chi Yip 24-Oct-2017

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Sods & Materials Engineering Co. 1 td.

Form No CARP156-2/Issue 1/Rev Cr01/05/2001

Appendix 5.1

Monitoring Schedules for Reporting Month and Coming Reporting Month

Contract No. HK/2015/01 Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3) Environmental Monitoring Schedule December 2017

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	27-Nov	28-Nov	29-Nov	30-Nov	1-Dec	2-Dec
			24hr TSP			
	Noise (daytime)			1hr TSP		
	Noise (daytille)					
3-Dec	4-Dec	5-Dec	6-Dec	7-Dec	8-Dec	9-Dec
		041 705				
		24hr TSP	1hr TSP			
	Noise (daytime)		1111 131			
	, ,					
10-Dec	11-Dec	12-Dec	13-Dec	14-Dec	15-Dec	16-Dec
	0.4h = TOD					0.4h = TOD
	24hr TSP	1hr TSP				24hr TSP
	Noise (daytime)	1111 101				
	, ,					
17-Dec	18-Dec	19-Dec	20-Dec	21-Dec	22-Dec	23-Dec
					24hr TSP	
	1hr TSP				24111 135	1hr TSP
				Noise (daytime)		
0.1.5						
24-Dec	25-Dec	26-Dec				

Contract No. HK/2015/01 Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3) Tentative Environmental Monitoring Schedule January 2018

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			27-Dec	28-Dec	29-Dec	30-Dec
				24hr TSP		
					1hr TSP	
			Noise (daytime)	Noise (daytime)		
31-Dec	1-Jan	2-Jan	3-Jan	4-Jan	5-Jan	6-Jan
			24hr TSP			
				1hr TSP		
		Noise (daytime)	Noise (daytime)			
7-Jan	8-Jan	9-Jan	10-Jan	11-Jan	12-Jan	13-Jan
		24hr TSP				24hr TSP
			1hr TSP			
	Noise (daytime)	Noise (daytime)				
14-Jan	15-Jan	16-Jan	17-Jan	18-Jan	19-Jan	20-Jan
					24hr TSP	
	1hr TSP					1hr TSP
	Noise (daytime)	Noise (daytime)				
21-Jan	22-Jan	23-Jan	24-Jan	25-Jan	26-Jan	
				24hr TSP		
					1hr TSP	
	Noise (daytime)	Noise (daytime)				

Appendix 5.2

Noise Monitoring Results and Graphical Presentations



Noise Monitoring Result for EP-376/2009

Day Time (0700 - 1900hrs on normal weekdays)

Location: M1a - Footbridge at EX-Wanchai Harbour Road Sports Centre


			Measur	ement Noi	se Level	Baseline Level	Construction Noise Level	Limit Level
Date	Time	Weather	Leq	L10	L90	Leq	Leq	Leq
						Unit: df	B(A), (30-min)	
27/11/17	15:00	Cloudy	76.5	78.5	72.3	73	74	75
4/12/17	13:45	Fine	79.1	81.5	75.1	73	78	75
11/12/17	10:15	Fine	77.9	80.2	74.2	73	76	75
21/12/17	14:15	Fine	76.0	78.1	72.9	73	73	75



Sampling, Field Measurement and Testing Works (Stage 3)

Graphic Presentation of Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

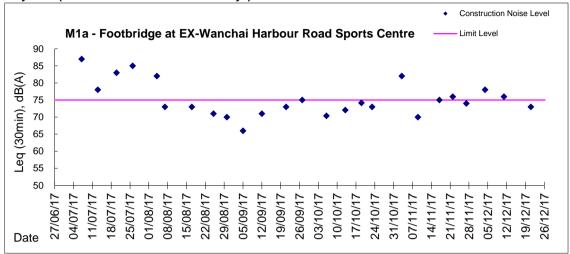

Appendix 5.3

Air Quality Monitoring Results and Graphical Presentations



Location: CMA5b - Pedestrian Plaza

Report on 24-hour TSP monitoring for EP-376/2009 Action Level - 209.9 μ g/m³ Limit Level - 260 μ g/m³

Date	Sampling	Weather	Filter paper	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /r	min	Total	TSP Level,
	Time	Condition	no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m³
29-Nov-17	8:00	Cloudy	22856	2.6499	2.8054	9416.31	9440.31	24.00	0.83	0.83	0.83	1199	129.7
5-Dec-17	8:00	Fine	23278	2.6733	2.9408	9443.31	9467.31	24.00	1.06	1.06	1.06	1526	175.3
11-Dec-17	8:00	Fine	23231	2.6716	2.9510	9470.31	9494.31	24.00	0.84	0.85	0.84	1215	229.9
16-Dec-17	8:00	Fine	23356	2.6772	2.8129	9497.31	9521.31	24.00	0.71	0.72	0.71	1029	131.9
22-Dec-17	8:00	Fine	23468	2.6225	2.8533	9524.31	9548.31	24.00	0.99	0.99	0.99	1426	161.8

Report on 1-hour TSP monitoring for EP-376/2009 Action Level - 339.7 μ g/m3 Limit Level - 500 μ g/m3

Date	Sampling	Weather	Filter paper	Filter Weigh	ıt, g	Elapse Time	e, hr	Sampling	Flo	w Rate, m ³ /r	min	Total	TSP Level,
	Time	Condition	no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m³
30-Nov-17	8:45	Cloudy	23153	2.6774	2.6843	9440.31	9441.31	1.00	0.83	0.80	0.82	49	140.8
30-Nov-17	10:50	Cloudy	23160	2.6703	2.6807	9441.31	9442.31	1.00	0.83	0.80	0.82	49	212.2
30-Nov-17	13:00	Cloudy	23166	2.6587	2.6797	9442.31	9443.31	1.00	1.09	1.05	1.07	64	327.9
6-Dec-17	8:50	Fine	23238	2.6637	2.6780	9467.31	9468.31	1.00	0.84	0.84	0.84	51	282.6
6-Dec-17	13:00	Fine	23263	2.7022	2.7155	9468.31	9469.31	1.00	0.84	0.84	0.84	51	262.8
6-Dec-17	14:05	Fine	23268	2.6678	2.6831	9469.31	9470.31	1.00	0.84	0.84	0.84	51	302.3
12-Dec-17	9:30	Cloudy	22845	2.6534	2.6770	9494.31	9495.31	1.00	0.99	0.99	0.99	59	397.6
12-Dec-17	10:45	Cloudy	22846	2.6896	2.7036	9495.31	9496.31	1.00	0.85	0.81	0.83	50	282.1
12-Dec-17	13:00	Cloudy	23366	2.6648	2.6762	9496.31	9497.31	1.00	0.85	0.85	0.85	51	224.8
18-Dec-17	8:50	Fine	23486	2.6056	2.6103	9521.31	9522.31	1.00	0.86	0.86	0.86	52	90.8
18-Dec-17	10:10	Fine	23479	2.6108	2.6230	9522.31	9523.31	1.00	0.86	0.86	0.86	52	235.6
18-Dec-17	13:50	Fine	23472	2.6069	2.6249	9523.31	9524.31	1.00	1.01	1.01	1.01	61	297.3
23-Dec-17	8:50	Fine	23434	2.6231	2.6366	9548.31	9549.31	1.00	1.02	1.02	1.02	61	220.0
23-Dec-17	9:55	Fine	23575	2.6027	2.6247	9549.31	9550.31	1.00	1.02	1.02	1.02	61	358.6
23-Dec-17	11:00	Fine	23568	2.6256	2.6371	9550.31	9551.31	1.00	1.02	1.02	1.02	61	187.4



Location: CMA6a - WDII PRE Office

Report on 24-hour TSP monitoring for EP-376/2009

Action Level - 207.1 μ g/m³ Limit Level - 260 μ g/m³

Date	Sampling	Weather	Filter	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /ı	min	Total	TSP Level,
	Time	Condition	paper no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m³
29-Nov-17	8:00	Cloudy	22861	2.6642	2.7353	3119.21	3143.21	24.00	1.06	1.06	1.06	1525	46.6
5-Dec-17	8:00	Fine	23276	2.6811	2.8237	3146.21	3170.21	24.00	1.07	1.07	1.07	1540	92.6
11-Dec-17	8:00	Fine	23379	2.6572	2.8086	3173.21	3197.21	24.00	1.07	1.07	1.07	1540	98.3
16-Dec-17	8:00	Fine	23350	2.6753	2.8115	3202.23	3226.23	24.00	1.08	1.09	1.08	1561	87.2
22-Dec-17	8:00	Fine	23469	2.6131	2.7572	3229.23	3253.23	24.00	1.07	1.07	1.07	1543	93.4


Report on 1-hour TSP monitoring for EP-376/2009

Action Level - 333 μg/m3 Limit Level - 500 μg/m3


Date	Sampling	Weather	Filter	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /	min	Total	TSP Level,
	Time	Condition	paper no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m³
30-Nov-17	8:45	Cloudy	23179	2.6872	2.6904	3143.21	3144.21	1.00	1.06	1.06	1.06	64	50.3
30-Nov-17	10:49	Cloudy	23285	2.6886	2.6932	3144.21	3145.21	1.00	1.06	1.06	1.06	64	72.3
30-Nov-17	13:00	Cloudy	23167	2.6646	2.6687	3145.21	3146.21	1.00	1.06	1.06	1.06	64	64.4
6-Dec-17	10:55	Fine	23265	2.6741	2.6803	3170.21	3171.21	1.00	1.07	1.07	1.07	64	96.7
6-Dec-17	13:00	Fine	23269	2.6712	2.6818	3171.21	3172.21	1.00	1.07	1.07	1.07	64	165.3
6-Dec-17	15:00	Fine	23237	2.6856	2.6967	3172.21	3173.21	1.00	1.07	1.07	1.07	64	173.1
12-Dec-17	9:40	Cloudy	23375	2.6692	2.6747	3199.21	3200.21	1.00	1.00	1.00	1.00	60	91.3
12-Dec-17	10:50	Cloudy	22840	2.6432	2.6470	3200.21	3201.21	1.00	1.00	1.00	1.00	60	63.1
12-Dec-17	13:00	Cloudy	23365	2.6776	2.6823	3201.21	3202.21	1.00	1.07	1.07	1.07	64	73.2
18-Dec-17	8:45	Fine	23484	2.5935	2.6029	3226.23	3227.23	1.00	1.09	1.09	1.09	65	144.1
18-Dec-17	10:25	Fine	23478	2.6190	2.6269	3227.23	3228.23	1.00	1.09	1.09	1.09	65	121.1
18-Dec-17	13:00	Fine	23390	2.6703	2.6793	3228.23	3229.23	1.00	1.09	1.09	1.09	65	138.0
23-Dec-17	8:50	Fine	23578	2.6074	2.6162	3253.23	3254.23	1.00	1.07	1.07	1.07	64	137.3
23-Dec-17	9:58	Fine	23574	2.6108	2.6171	3254.23	3255.23	1.00	1.07	1.07	1.07	64	98.3
23-Dec-17	11:00	Fine	23567	2.6012	2.6072	3255.23	3256.23	1.00	1.07	1.07	1.07	64	93.6



Graphic Presentation of 1 hour TSP Result for EP-376/2009

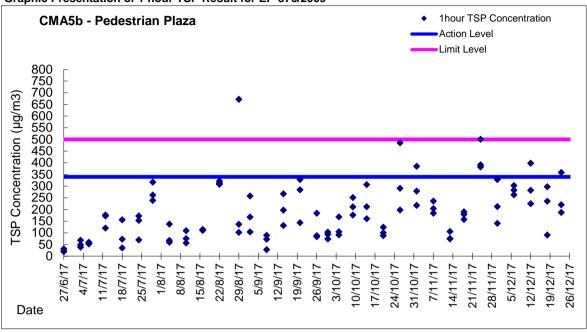



Graphic Presentation of 24 hour TSP Result for EP-376/2009

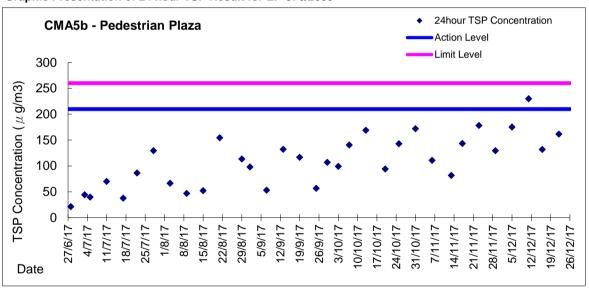



Graphic Presentation of 1 hour TSP Result for EP-376/2009

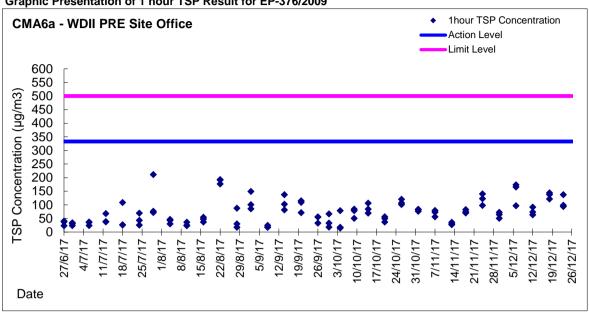

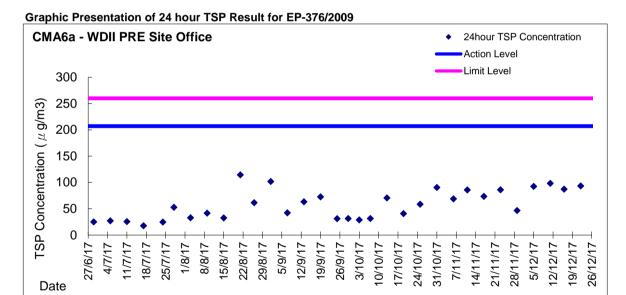

Appendix 6.1

Event Action Plans

Event/Action Plan for Construction Noise

EVENT		AC	CTION	
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	 Notify ER, IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, ER and Contractor; Discuss with the IEC and Contractor on remedial measures required; Increase monitoring frequency to check mitigation effectiveness. (The above actions should be taken within 2 working days after the exceedance is identified) 	1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Advise the ER on the effectiveness of the proposed remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	 Confirm receipt of notification of failure in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified) 	Submit noise mitigation proposals to IEC and ER; Implement noise mitigation proposals. (The above actions should be taken within 2 working days after the exceedance is identified)



EVENT		AC	CTION	
	ET	IEC	ER	CONTRACTOR
Limit Level being exceeded	 Inform IEC, ER, Contractor and EPD; Repeat measurements to confirm findings; Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contractor's working procedures; 6. Discuss with the IEC, Contractor and ER on remedial measures required; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified) 	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. (The above actions should be taken within 2 working days after the exceedance is identified)	 Confirm receipt of notification of failure in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures; If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. The above actions should be taken within 2 working days after the exceedance is identified) 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC and ER within 3 working days of notification; Implement the agreed proposals; Submit further proposal if problem still not under control; Stop the relevant portion of works as instructed by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)

Event / Action Dian for Construction Air Quality

FVENT		ACTION		
EVENT	ET	IEC	ER	CONTRACTOR
ACTION LEVEL				
Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; Increase monitoring frequency to daily. (The above actions should be taken within 2 working days after the exceedance is identified)	Check monitoring data submitted by ET; Check Contractor's working method. (The above actions should be taken within 2 working days after the exceedance is identified)	Notify Contractor. (The above actions should be taken within 2 working days after the exceedance is identified)	Rectify any unacceptable practice; Amend working methods if appropriate (The above actions should be taken within 2 working days after the exceedance is identified)
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Supervise Implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	Submit proposals for remedial to ER within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
LIMIT LEVEL				
Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. (The above actions should be taken within 2 working days after the exceedance is identified)	Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ER on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification 3. Implement the agreed proposals; Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
Exceedance for two or more consecutive samples	Notify IEC, ER, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring, (The above actions should be taken within 2 working days after the exceedance is identified)	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures.	Confirm receipt of notification of failure in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification 3. Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)



Event and Action Dian for Marine Water Quality

EVENT		ACTION		
	ET	IEC	ER	CONTRACTOR
Action level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agree mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Action level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next working day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Limit level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3working days; Implement the agreed mitigation measures; As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities. (The above actions should be taken within 1 working day after the exceedance is identified)

Event and Action Plan for Odour Patrol

Event	ACTION											
	Person-in-charge of Odour Monitoring	Implementation Agent Identified by CEDD										
Action Level												
Exceedance of Action Level	Identify source/reason of exceedance; Repeat odour patrol to confirm finding.	 Carry out investigation to identify the source/reason of exceedance; Rectify any unacceptable practice Implement more mitigation measures if necessary; Inform EPD or MD if exceedance is considered to be caused by expedient connections or floating debris. 										
Limit Level												
Exceedance of Limit Level	I. Identify source / reason of exceedance; Repeat odour patrol to confirm findings; Increase odour patrol frequency; If exceedance stops, cease additional odour patrol.	 Carry out investigation to identify the source/reason of exceedance. Investigation shall be completed within 2 weeks; Rectify any unacceptable practice; Formulate remedial actions; Ensure remedial actions properly implemented; If exceedance continues, consider what more/enhanced mitigation measures shall be implemented; Inform EPD or MD if exceedance is considered to be caused by expedient connections or floating debris. 										

Appendix 6.2

Summary for Notification of Exceedance

Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action	
X_16A072	11-Dec-17	8:00	CMA5b- Pedestrian Plaza	229.2	24hr TSP (ug/m³)	209.9	260	Possible reason:	TSP level potentially in relate to the ambient condition around the monitoring station.
	12-Dec-17	9:30	CMA5b- Pedestrian Plaza	397.6	1hr TSP (ug/m³)	339.7	500	Action taken / to be taken:	Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures.
								Remarks / Other Obs:	Road and drains works for P2 road was undertaken by the Contractor of HK/2012/08 around the monitoring location on the monitoring date and no particular observation regarding air quality impact was observed during sampling.
									Meanwhile, non WDII-CWB Project construction activities was observed opposite to the monitoring station on the monitoring date. According to the EPD monitoring record, AQHI recorded at the Causeaway Bay station was recorded as Lv4 - Lv7 on 11 Decmeber 2017 and recorded as Lv6 on 12 December 2017 during the monitoring period indicating the adverse ambient condition. In addition, similar elevation in TSP level were recorded across the same period on 11 December 2017 at other Project AQM stations including CMA6a at Wanchai and CMA3a at Causeway Bay area suggesting overall air quality within the district was under influence of ambient pollutant.
									In view of the above, the exceedance was considered to be not related to the Project works under Contract HK/2012/08 and potentially contributed by ambient air quality condition. Nevertheless, the Contractor of HK/2012/08 was advised to strengthen the overall dust suppression control measures to ensure all dusty surface are dampened to avoid potential dust emission.

Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action	
X_16A075	23-Dec-17	9:55	CMA5b- Pedestrian Plaza	358.6	1hr TSP (ug/m³)	339.7	500	Possible reason:	TSP level potentially in relate to the nearby traffic and ambient condition around the monitoring station at the time of monitoring.
								Action taken / to be taken:	Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures.
								Remarks / Other Obs:	Road and drains works for P2 road was undertaken by the Contractor of HK/2012/08 around the monitoring location on the monitoring date and no particular observation regarding air quality impact was observed during sampling. Meanwhile, non WDII-CWB Project excavation material handling was observed opposite to the monitoring station on the monitoring date. In addition, elevated PM2.5 and PM10 level were recorded at the EPD Causeway Bay monitoring station across the monitoring period suggesting the meterological condition at the time of monitoring may not favour the dispersion of ambient air pollutant within the district and hence affecting the air quality.
									In view of the above, the exceedance was considered to be not related to the Project works under Contract HK/2012/08 and potentially contributed by ambient air quality condition. Nevertheless, the Contractor of HK/2012/08 was advised to strengthen the overall dust suppression control measures to ensure all dusty surface are dampened to avoid potential dust emission.

Ref. No.	Date	Time	Location	Construction Noise Level, dB(A)	Parameter	Action Level	Limit Level dB(A)	Follow-up action	
X_16N108	4-Dec-17	13:45	M1a-Footbridge at Ex Harbour Road Sports Centre	78	Leq(30min)	when one documented complaint was received.	75	Possible reason:	Non WDII-CWB excavation works and hammering immeidately next to the monitoring station was observed as the major noise contribution during monitoring.
								Action taken / to be taken:	A repeat measurement was conducted to confirm result and reviewed the trend of previous noise monitoring and Contractor's working procedure.
								Remarks / Other Obs:	No construction work under EP-376/2009 was conducted by Contract HK/2012/08 around the concerned location during the time of measurement while non WDII-CWB excavation and hammering works immeidately next to the monitoring station was observed as the major noise contribution during monitoring. As such, the exceedance was considered as not related to Project works under Contract HK/2012/08 Project.

Ref. No.	Date	Time	Location	Construction Noise Level, dB(A)	Parameter	Action Level	Limit Level dB(A)	Follow-up action	
X_16N112	11-Dec-17	10:15	M1a-Footbridge at Ex Harbour Road Sports Centre	77	Leq(30min)	when one documented complaint was received.	75	Possible reason:	Non WDII-CWB excavation and continuous breaking works immediately next to the monitoring station were observed as the major noise contribution during monitoring
								Action taken / to be taken:	A repeat measurement was conducted to confirm result and reviewed the trend of previous noise monitoring and Contractor's working procedure.
								Remarks / Other Obs:	No construction work under EP-376/2009 was conducted by Contract HK/2012/08 around the concerned location during the time of measurement while non WDII-CWB excavation and continuous breaking works immediately next to the monitoring station were observed as the major noise contribution during monitoring. As such, the exceedance was considered as not relate to Project works under HK/2012/08.

Appendix 9.1

Complaint Log

Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					ł	


Appendix 10.1

Construction Programme of Individual Contracts



CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central - Wan Chai Bypass at Wan Chai West

Page : 1 / 5

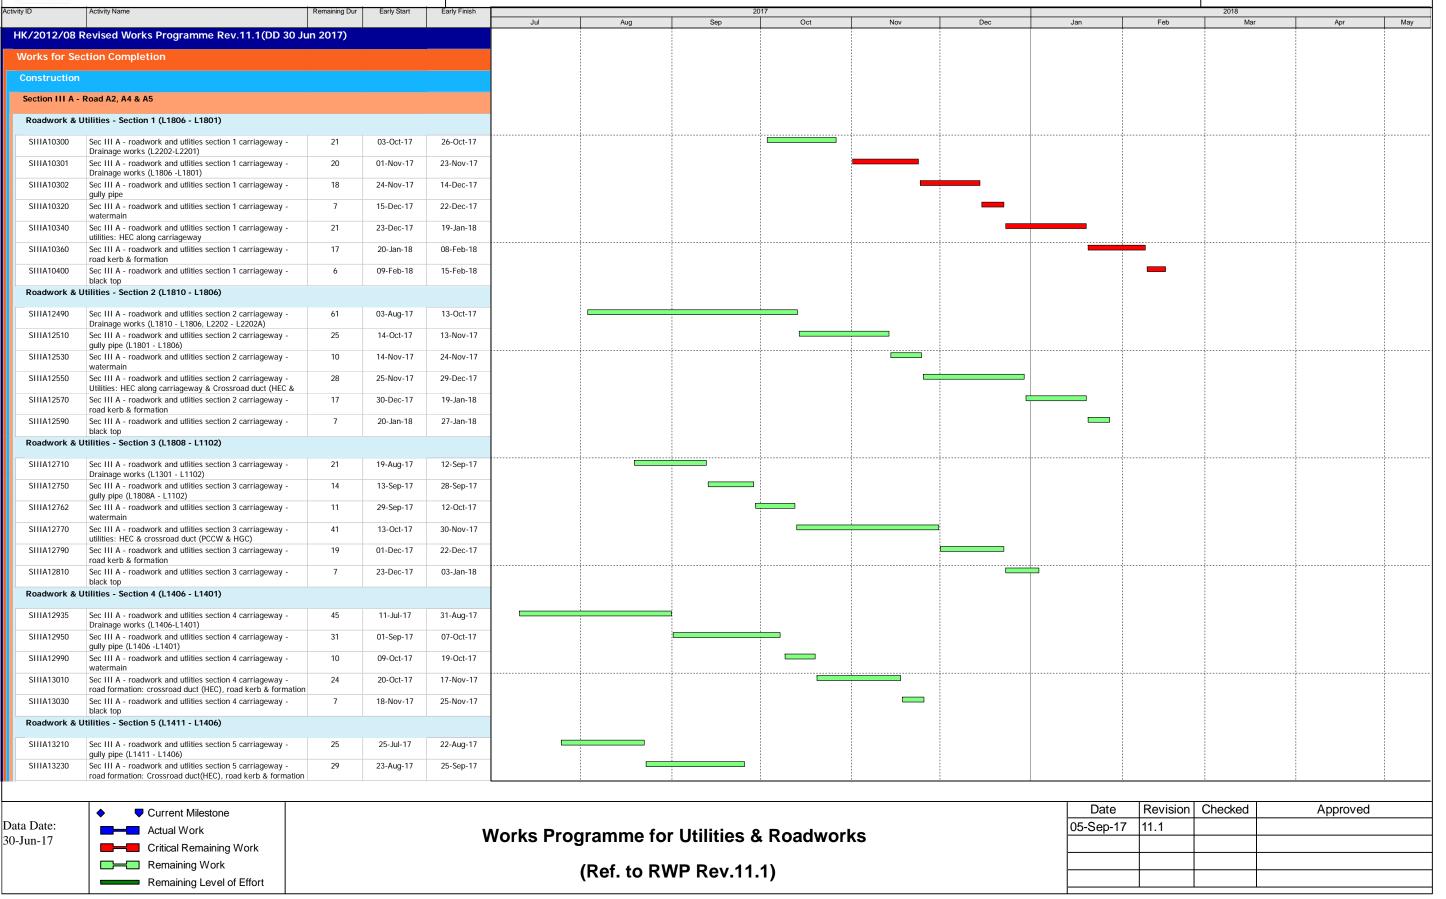



CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central - Wan Chai Bypass at Wan Chai West

Page: 2 / 5

	OHNAOTATE EEA							опаг Буразз с							
tivity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Jul	Aug	Sep 20	017 Oct	Nov	Dec	Jan	Feb	2018 Mar	Apr	May
SIIIA13250	Sec III A - roadwork and utilities section 5 carriageway - black top	7	26-Sep-17	04-Oct-17											
Roadwork & l	Utilities - Section 6 (L1102 - L1411)														
SIIIA13372	Sec III A - roadwork and utilities section 6 carriageway - Backfilling of water channel adjacent culvert K bay 16	14	18-Aug-17	02-Sep-17			-								
SIIIA13373	Sec III A - roadwork and utilities section 6 carriageway -	20	24-Aug-17	15-Sep-17		_									
SIIIA13380	Backfilling of water channel from culvert K bay 16 to 20B Sec III A - roadwork and utilities section 6 carriageway -	9	16-Sep-17	26-Sep-17											
SIIIA13385	Removal of temporary water channel Sec III A - roadwork and utilities section 6 carriageway -	6	27-Sep-17	04-Oct-17			_								-
SIIIA13389	Waterproofing for tunnel roof slab Sec III A - roadwork and utilities section 6 carriageway -	5	05-Oct-17	10-Oct-17				_							
SIIIA13395	Backfilling above tunnel roof slab Sec III A - roadwork and utilities section 6 carriageway -	9	11-Oct-17	20-Oct-17											
SIIIA13399	Drainage works (L1101-L1102) Sec III A - roadwork and utilities section 6 carriageway -	8	21-Oct-17	31-Oct-17											
SIIIA13430	gully pipe (L1101 -L1102) Sec III A - roadwork and utilities section 6 carriageway -	30	03-Aug-17	06-Sep-17											
SIIIA13444	gully pipe (Culvert L - L1411) Sec III A - roadwork and utilities section 6 carriageway -	7	07-Sep-17	14-Sep-17											
SIIIA13445	watermain Sec III A - roadwork and utilities section 6 carriageway -	14	15-Sep-17	30-Sep-17											
SIIIA13450	utilities: HEC , HGC, PCCW Sec III A - roadwork and utilities section 6 carriageway -	18	01-Nov-17	21-Nov-17				_							
SIIIA13470	road kerb & formation Sec III A - roadwork and utlities section 6 carriageway -	7	22-Nov-17	29-Nov-17											
Section V - Roa	black top														
Roadwork & U															
Section 1 (L15															
SV12450		64	27-Jul-17	10-Oct-17	_										
	Sec V - Roadwork & Utilities Section 1 Carriageway - Gully pipe (L1903 - L1906, L1501-L1504)				_				1						
SV12460	Sec V - Roadwork & Utilities Section 1 Carriageway - Utilities (TCSS crossroad duct)		11-Oct-17	04-Nov-17						Ļ					
SV12490	Sec V - Roadwork & Utilities Section 1 Carriageway - Road kerb & formation		06-Nov-17	02-Dec-17											
SV12520	Sec V - Roadwork & Utilities Section 1 Carriageway - Black top	20	04-Dec-17	28-Dec-17											
SV12540	Sec V - Roadwork & Utilities Section 1 footpath - Watermain	14	06-Nov-17	21-Nov-17											
SV12570	Sec V - Roadwork & Utilities Section 1 footpath - utilities:TCSS	30	22-Nov-17	28-Dec-17											
SV12580	Sec V - Roadwork & Utilities Section 1 footpath - paving block	30	29-Dec-17	02-Feb-18						_					
Section 2 (L1	1510 - L1504)														
SV12602	Sec V - Roadwork & Utilities Section 2 Carriageway : Backfilling	7	18-Aug-17	25-Aug-17											
SV12603	Sec V - Roadwork & Utilities Section 2 Carriageway - Gully pipe (L1501 - L1507 & L1611 - L1609)	30	26-Aug-17	29-Sep-17		-									
SV12604	Sec V - Roadwork & Utilities Section 2 Carriageway : formation for access diversion	6	30-Sep-17	07-Oct-17			1								
SV12606	Sec V - Roadwork & Utilities Section 2 Carriageway: Divert access cross Zone B	0	09-Oct-17					•							
SV12610	Sec V - Roadwork & Utilities Section 2 Carriageway - Drainage Works L1507-L1504)	31	09-Oct-17	14-Nov-17											
SV12630	Sec V - Roadwork & Utilities Section 2 Carriageway - Drainage Works L1406A - L1406B	21	15-Nov-17	08-Dec-17						<u> </u>					
SV12665	Sec V - Roadwork & Utilities Section 2 Carriageway - Gully pipe (L1507-L1504, L1406A)	25	09-Dec-17	10-Jan-18											
SV12666	Sec V - Roadwork & Utilities Section 2 Carriageway - Utilities: HEC crossroad duct	11	11-Jan-18	23-Jan-18											
SV12670	Sec V - Roadwork & Utilities Section 2 Carriageway - Road kerb & formation	21	24-Jan-18	20-Feb-18							_				
SV12680	Sec V - Roadwork & Utilities Section 2 Carriageway - Black	20	21-Feb-18	15-Mar-18											
SV12690	top Sec V - Roadwork & Utilities Section 2 footpath - Drainage	25	09-Dec-17	10-Jan-18											
SV12695	Works (L2104 - L2105) Sec V - Roadwork & Utilities Section 2 footpath - Watermain	18	11-Jan-18	31-Jan-18						! ! ! !					
SV12700	Sec V - Roadwork & Utilities Section 2 footpath - utilities:	16	01-Feb-18	22-Feb-18											
	TCSS Sec V - Roadwork & Utilities Section 2 footpath - paving	18	23-Feb-18	15-Mar-18								_			
SV12740	See V Roadwork & Clinics Section 2 rootpath paving									i company and a second a second and a second a second and	I .	· ·	i .	i contract of the contract of	



CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central - Wan Chai Bypass at Wan Chai West

Page: 3 / 5

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish			_	017					2018		
SIV12765	Sec V - Roadwork & Utilities Section 3 Carriageway -	25	16-Aug-17*	13-Sep-17	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
SIV12766	Demolish D wall Sec V - Roadwork & Utilities Section 3 Carriageway -	14	28-Sep-17	14-Oct-17		1 1 1 1 1 1									
SIV12810	Drainage Works (Culvert L - L1611) Sec V - Roadwork & Utilities Section 3 Carriageway - Gully	30	16-Oct-17	20-Nov-17											
SIV12815	pipe (Culvert L - L1611) Sec V - Roadwork & Utilities Section 3 Carriageway - Road	24	21-Nov-17	18-Dec-17											1
SIV12820	kerb & formation Sec V - Roadwork & Utilities Section 3 Carriageway - Black	20	19-Dec-17	13-Jan-18											1
SIV12840	Sec V - Roadwork & Utilities footpath - Drainage works	25	16-Oct-17	14-Nov-17											
SIV12844	(Culvert L - L2105) Sec V - Roadwork & Utilities Section 3 footpath - U channel	21	15-Nov-17	08-Dec-17						:					
SIV12850	Sec V - Roadwork & Utilities footpath - Watermain	21	15-Nov-17	08-Dec-17											
SIV12855	Sec V - Utilities: HEC (80m at site access) to MVB Plant Room - 1st stage excavation	10	15-Jul-17*	26-Jul-17											
SIV12857	Sec V - Utilities: HEC (80m at site access) to MVB Plant Room - 2nd stag excavation	10	08-Aug-17	18-Aug-17											
SIV12859	Sec V - Utilities: HEC (80m at site access) to MVB Plant Room - cabling	12	25-Aug-17	07-Sep-17											
SIV12860	Sec V - Roadwork & Utilities Section 3 footpath - Utilities: TCSS, HGC, PCCW)	39	09-Dec-17	26-Jan-18		; ; ; ; ; ;									
SIV12880	Sec V - Roadwork & Utilities Section 3 footpath - Paving block	22	27-Jan-18	24-Feb-18											
Section 4 (K1	106 - Culvert L)					 									
SIV12282	Sec V - Roadwork & Utilities Section 4 Carriageway - Drainage Works (K1311 - Culvert K, L1201, L1301)	31	16-Sep-17	23-Oct-17											
SIV12300	Sec V - Roadwork & Utilities Section 4 Carriageway - Gully pipe (K1106-Culvert K, K1201-Culvert K, L1201, L1301)	35	24-Oct-17	04-Dec-17											
SIV12305	Sec V - Roadwork & Utilities Section 4 Carriageway - Utilities : crossroad duct	14	05-Dec-17	20-Dec-17											
SIV12310	Sec V - Roadwork & Utilities Section 4 Carriageway - Road kerb & formation	24	02-Jan-18	29-Jan-18											1
SIV12320	Sec V - Roadwork & Utilities Section 4 Carriageway - Black top	20	30-Jan-18	24-Feb-18											1
SIV12360	Sec V - Roadwork & Utilities Section 4 Carriageway - watermain	15	21-Dec-17	10-Jan-18											
SIV12380	Sec V - Utilities: HEC (50m at water channel) to MVB plant room - Excavation	10	22-Aug-17	01-Sep-17											
SIV12400	Sec V - Utilities: HEC (50m at water channel) to MVB plant room - Cabling	9	08-Sep-17	18-Sep-17											
SIV12420	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : TCSS	21	11-Jan-18	03-Feb-18											1
SIV12440	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : HGC & PCCW	8	21-Dec-17	02-Jan-18											1
SIV12460	Sec V - Roadwork & Utilities Section 4 footpath - Paving block	22	05-Feb-18	05-Mar-18											
Section IV - S															
Roadwork &	Utilities														
Section 1 (L1	6608 - L1601)														
SIV11750	Sec IV - Roadworks & Utilites at SR3 Section 1 Carriageway - Sewerage works	14	16-Sep-17	03-Oct-17				=							
SIV11760	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L1607-L1601, L2004-L2005)		16-Sep-17	02-Nov-17											
SIV11762	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Drainage Works (L2103-L2101)		03-Nov-17	27-Nov-17											
SIV11764	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Gully pipe (L1607-L1601, L2004-L2005)	25	28-Nov-17	28-Dec-17					-	_					
SIV11780	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Watermain	18	29-Dec-17	19-Jan-18						_					1
SIV11800	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Utilities : TCSS crossroad duct	14	20-Jan-18	05-Feb-18		; ; ; ; ; ;									
SIV11830	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Road kerb & formation	24	06-Feb-18	08-Mar-18			-								
SIV11840 SIV11860	Sec IV - Roadwork & Utilities at SR3 Section 1 Carriageway - Black top Sec IV - Roadwork & Utilities at SR3 Section 1 footpath -	7	09-Mar-18 29-Dec-17	21-Mar-18 06-Jan-18						_					
SIV11880	Drainage Works: future connection pipes Sec IV - Roadwork & Utilities at SR3 Section 1 footpath -	7	08-Jan-18	15-Jan-18						_					
SIV11880 SIV11900	watermain Sec IV - Roadwork & Utilities at SR3 Section 1 footpath -	39	16-Jan-18	05-Mar-18											
SIV11900	utilities: HEC & TCSS Sec IV - Roadwork & Utilities at SR3 Section 1 footpath -	17	06-Mar-18	24-Mar-18									-		
31711720	paving block	17	OO-IVIAI * 10	27-IVIGI = 10			<u> </u>			İ					



CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central - Wan Chai Bypass at Wan Chai West

Page: 4 / 5

DUDLU	CHINA STATE - LEA	NDEK JOIN	VENTURE			C	entrai - wan	Chai Bypass	s at wan Cha	ai west					
Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Jul	Aug	20 Sep	17 Oct	Nov	Dec	Jan	Feb	2018 Mar	Apr	May
Section 2 (L	2301 - L2103)				Jul	Aug	oeh	Oct	INOV	Dec	Jan	reb	ivial	Api	iviay
SIV11940	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Drainage Works (L2301-L2103)	- 21	23-Sep-17	18-Oct-17											
SIV11941	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Drainage Works (L608-L1609)	- 30	19-Oct-17	23-Nov-17									; ; ; ; ;		
SIV11942	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Gully pipe (L2301-L2013, L1608-L1609)	- 22	24-Nov-17	19-Dec-17									1 1 1 1 1		
SIV11960	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Watermain	- 10	20-Dec-17	03-Jan-18											
SIV11970	Sec IV - Utilities: HEC (40m crossing) to MVB plant room - excavation	10	27-Jul-17	07-Aug-17					j) 	j		
SIV11975	Sec IV - Utilities: HEC (40m crossing) to MVB plant room - cabling	5	19-Aug-17	24-Aug-17								1 1 1 1 1	1 1 1 1 1		
SIV11980	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Utilities: TCSS crossroad duct)	- 14	04-Jan-18	19-Jan-18											
SIV12010	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Road kerb & formation		20-Dec-17	19-Jan-18									 		
SIV12020	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Black top	. 7	20-Jan-18	27-Jan-18									 		
SIV12040	Sec IV - Roadwork & Utilities at SR3 Section 2 footpath - Drainage Works: future connection pipes	7	04-Jan-18	11-Jan-18									1 1 1 1 1		
SIV12060	Sec IV - Roadwork & Utilities at SR3 Section 2 footpath - utilities: TCSS	25	12-Jan-18	09-Feb-18											
SIV12080	Sec IV - Roadwork & Utilities at SR3 Section 2 footpath - paving block	21	10-Feb-18	09-Mar-18											
Section 3 (N	//H1.6 - L2301)														
SIV12100	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Drainage Works (M/H1.7 - L2301)		19-Oct-17	24-Nov-17									 		
SIV12102	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: Demolish seawall		23-Sep-17	17-Oct-17								! ! !	1 1 1 1 1		
SIV12103	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: ELS		18-Oct-17	30-Oct-17											
SIV12104 SIV12105	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - M1.7-M1.6: Construct manhole & pipes Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -		31-Oct-17 12-Dec-17	11-Dec-17 27-Dec-17					 			1	1 1 1 1 1 1		
SIV12105	M1.7-M1.6: backfilling & divert EVA Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -		28-Dec-17	30-Jan-18											
SIV12120	Drainage Works (M1.6-C1.1-C1.2): Construct MH and pipes Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -		31-Jan-18	13-Feb-18											
SIV12122	Drainage Works (M1.6-C1.1-C1.2): Backfilling & shift lane Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -		14-Feb-18	28-Feb-18											
SIV12138	Drainage Works (M1.6-C1.1-C1.2): Construct MH C1.2 Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway	38	20-Jul-17*	01-Sep-17]								
SIV12140	-Utilities: HEC to MVB Plant room - cabling Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	- 30	25-Nov-17	02-Jan-18											
SIV12150	Gully pipe (M/H 1.7 - L2301) Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	- 14	03-Jan-18	18-Jan-18											
SIV12155	Road kerb Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	- 10	01-Mar-18	12-Mar-18								 			
SIV12160	formation Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway - Black top	- 10	13-Mar-18	23-Mar-18											
SIV12165	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath -Utilities: HEC to MVB Plant room - cabling	21	02-Sep-17	26-Sep-17											
SIV12170	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Utilities: TCSS	22	27-Sep-17	23-Oct-17								1 1 1 1 1 1	1 		
SIV12180	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - U channel	14	24-Oct-17	09-Nov-17											
SIV12220	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Paving block	45	10-Nov-17	04-Jan-18											
Section VII -	Remainder Works														
Road & Drain	nage Works (Culvert L - M/H1.7, Adjacent to SR3)														
SVII11600	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Drainage Works (Culvert L -MH1.7)	40	12-Dec-17	30-Jan-18								: ! ! ! !	: 		
SVII11640	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Gully pipe (Culvert L -MH1.7)	- 27	31-Jan-18	06-Mar-18								i i			
SVII11650	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - TCSS duct , road kerb & formation	- 21	07-Mar-18	30-Mar-18											
SVII11660	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Black top	6	31-Mar-18	07-Apr-18											
SVII11680	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - U channel	14	07-Mar-18	22-Mar-18								: ! ! ! !			
SVII11700	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - utilities	13	23-Mar-18	07-Apr-18								1 1 1 1 1			
SVII11720	Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - paving block	11	09-Apr-18	24-Apr-18								! ! !	1 1 1 1 1		



CEDD Contract No. HK/2012/08 **Wan Chai Development Phase II** Central - Wan Chai Bypass at Wan Chai West

Page: 5 / 5

