CONTRACT NO: HK/2015/01

WANCHAI DEVELOPMENT PHASE II AND CENTRAL WANCHAI BYPASS SAMPLING, FIELD MEASUREMENT AND TESTING WORK (STAGE 3)

ENVIRONMENTAL PERMIT NO. EP-376/2009, FURTHER ENVIRONMENTAL PERMITS NO. FEP-01/376/2009 AND FEP-02/376/2009

MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT

- JUNE 2019 -

CLIENTS:

Civil Engineering and Development Department

PREPARED BY:

Lam Geotechnics Limited

11/F Centre Point 181-185 Gloucester Road, Wanchai, H.K.

Telephone: (852) 2882-3939
Facsimile: (852) 2882-3331
E-mail: info@lamenviro.com
Website: http://www.lamenviro.com

CERTIFIED BY:

Raymond Dai

Environmental Team Leader

DATE:

10 July 2019



Ref.: AACWBIECEM00_0_11467L.19

10 July 2019

By Post and Fax (2691 2649)

AECOM Asia Company Limited 11/F Tower 2 Grand Central Plaza 138 Shatin Rural Committee Road Shatin New Territories Hong Kong

Attention: Mr. Conrad Ng

Dear Mr. Ng,

Re: Wan Chai Development Phase II - Central-Wan Chai Bypass

Monthly Environmental Monitoring and Audit Report (June 2019)
for EP-376/2009, FEP-01/376/2009 and FEP-02/376/2009

Reference is made to the Environmental Team's submission of the captioned Monthly Environmental Monitoring and Audit (EM&A) Report for June 2019 received by e-mail on 10 July 2019 for our review and comment.

Please be informed that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 in the captioned Environmental Permit.

Thank you very much for your attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,

David Yeung

Independent Environmental Checker

c.c. CEDD Attn: Mr. Lee Hon by fax: 2301 1277

AECOM Attn: Ms. Gloria Tang by fax: 2587 1877
AECOM Attn: Mr. Francis Leong/ Stephen Lai by fax: 2691 2649
Lam Attn: Mr. Raymond Dai by fax: 2882 3331

Q:\Projects\AACWBIECEM00\Corr\AACWBIECEM00_0_11467L.19.docx



TABLE OF CONTENTS

EXE	ECUTIV	VE SUMMARY	3
1	INTR	ODUCTION	5
	1.1 1.2	Scope of the Report Structure of the Report	
2	PRO.	JECT BACKGROUND	7
	2.1 2.2 2.3	Background Scope of the Project and Site Description Project Organization and Contact Personnel	7
3	STAT	TUS OF REGULATORY COMPLIANCE	9
	3.1	Status of Environmental Licensing and Permitting under the Project	9
4	MON	ITORING REQUIREMENTS	11
	4.1 4.2	Noise MonitoringAir Quality Monitoring	
5	MON	ITORING RESULTS	14
	5.1 5.2 5.3	Noise Monitoring Results	15
6	COM	PLIANCE AUDIT	16
	6.1 6.2 6.3 6.4	Noise Monitoring	16 16
7 PRC		ULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT S	
8	ENV	IRONMENTAL SITE AUDIT	17
9	COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION 19		
10	CONCLUSION 20		



LIST OF TABLES

Table 2.1	Schedule 2 Designated Projects under this Project
Table 2.2	Contact Details of Key Personnel
Table 3.1	Summary of the current status on licences and/or permits on environmental
	protection pertinent to the Project
Table 3.2	Cumulative Summary of Valid Licences and Permits under Contract no. HK/2012/08
Table 3.3	Summary of submission status under FEP-01/376/2009 Condition
Table 4.1	Noise Monitoring Stations
Table 4.2	Air Quality Monitoring Stations
Table 5.1	Noise Monitoring Stations for Contract no. HK/2012/08
Table 5.2	Air Quality Monitoring Station for Contract no. HK/2012/08
Table 5.3	Details of Waste Disposal for Contract no. HK/2012/08
Table 8.1	Summary of Environmental Inspections for Contract no. HK/2012/08
Table 9.1	Cumulative Statistics on Complaints
Table 9.2	Cumulative Statistics on Successful Prosecutions
Table 10.1	Summary of Key Construction Activities of Individual Contract(s) to be
<u> </u>	commenced in Coming Reporting Month

LIST OF FIGURES

Figure 2.1	Project Layout
Figure 2.2	Project Organization Chart
Figure 4.1	Locations of Environmental Monitoring Stations

LIST OF APPENDICES

in DioLo
Environmental Mitigation Implementation Schedule
Action and Limit Level
Monitoring Schedule for Reporting Month and Coming month
Noise Monitoring Results and Graphical Presentations
Air Quality Monitoring Results and Graphical Presentations
Event Action Plans
Notification of Exceedance
Complaint Log
Construction Programme of Individual Contracts



EXECUTIVE SUMMARY

- i. This is the Environmental Monitoring and Audit (EM&A) Monthly Report June 2019 specific for Environmental Permit no. EP-376/2009 and Further Environmental Permits no. FEP-01/376/2009 and FEP-02/376/2009. The EM&A report is prepared by the Environmental Team (ET) employed under Contract No. HK/2015/01 Wan Chai Development Phase II and Central Wanchai Bypass Sampling, Field Measurement and Testing Works (Stage 3). This report presents the environmental monitoring findings and information recorded during the period of 27th May 2019 to 26th June 2019. The cut-off date of reporting is at 26th of each reporting month.
- ii. In the reporting month, the principal work activities of the contract are included as follows:
 Contract no. HK/2012/08 Wan Chai Development Phase II Central- Wan Chai Bypass at Wan Chai West
 - Landscaping

Noise Monitoring

- iii. Noise monitoring was conducted at M1a Harbour Road Sports Centre.
- iv. With respect to the shift in major construction site portions at Wan Chai North, the noise monitoring station M1a – Harbour Road Sports Centre was finely adjusted from East of Harbour Road Sports Centre to West of Harbour Road Sports Centre on 21 June 2016.
- v. With respect to the demolition of Ex-Harbour Road Sports Centre, the respective noise monitoring station M1a Harbour Road Sports Centre were finely adjusted on 16 and 25 May 2017 and thereafter to the Footbridge for Harbour Road Sports for noise monitoring.
- vi. With respect to WDII RSS confirmed that the remaining works under HK/2012/08 would be tree planting works at EP-376/2009 area only, considered that no adverse noise impact would be contributed by the tree planting works, the respective noise monitoring at noise monitoring station M1a Footbridge at EX-Wanchai Harbour Road Sports Centre was temporary suspended from 27 March 2019 onwards.

Air Quality Monitoring

- vii. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted on every six days basis at CMA5b Pedestrian Plaza and CMA6a Contractor HK/2012/08 Site Office.
- viii. With respect to WDII RSS confirmed that the remaining works under HK/2012/08 would be tree planting works at EP-376/2009 area only, considered that no adverse air quality impact would be contributed by the tree planting works, the respective air quality monitoring at monitoring stations CMA5b Pedestrian Plaza and CMA6a Contractor HK/2012/08 Site Office, were temporary suspended from 27 March 2019 onwards.



Complaints, Notifications of Summons and Successful Prosecutions

ix. No environmental complaint was received in this reporting month.

Site Inspections and Audit

x. The Environmental Team (ET) conducted weekly site inspection for Contract no. HK/2012/08 in this reporting period. The Contractors rectified major observations and recommendations made during the audit sessions. No non-conformance was identified during the site inspections.

Future Key Issues

xi. In the coming reporting month, the principal work activities of the contract is anticipated as follows:

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West</u>

Landscaping



1 INTRODUCTION

1.1 Scope of the Report

1.1.1. Lam Geotechnics Limited (LGL) has been appointed take up the role as the Environmental Team (ET) under Environmental Permit no. EP-376/2009 and Further Environmental Permits no. FEP-01/376/2009 and FEP-02/376/2009 to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Wan Chai Development Phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008).

This report documents the finding of EM&A works for Environmental Permit (EP) no. EP-376/2009 and Further Environmental Permits no. FEP-01/376/2009 and FEP-02/376/2009, during the period of 27th May 2019 to 26th June 2019. The cut-off date of reporting is the 26th of each reporting month.

1.2 Structure of the Report

Section 1 *Introduction* – details the scope and structure of the report.

Section 2 *Project Background* – summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.

Section 3 Status of Regulatory Compliance – summarizes the status of valid Environmental Permits / Licenses during the reporting period.

Section 4 *Monitoring Requirements* – summarizes all monitoring parameters, monitoring methodology and equipment, monitoring locations, monitoring frequency, criteria and respective event and action plan and monitoring programmes.

Section 5 Monitoring Results – summarizes the monitoring results obtained in the reporting period.

Section 6 Compliance Audit – summarizes the auditing of monitoring results, all exceedances environmental parameters.

Section 7 Cumulative Construction Impact due to the Concurrent Projects – summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.



Section 8	Environmental Site Audit – summarizes the findings of weekly site
	inspections undertaken within the reporting period, with a review of any
	relevant follow-up actions within the reporting period.

Section 9 Complaints, Notification of summons and Prosecution – summarizes the cumulative statistics on complaints, notification of summons and prosecution

Section 10 Conclusion



2 PROJECT BACKGROUND

2.1 Background

2.1.1 Wan Chai Development phase II and Central-Wan Chai Bypass (hereafter called "the Project") are Designated Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Report for Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) has been approved on 11 December 2008.

2.2 Scope of the Project and Site Description

- 2.2.1. The design and construction of Wan Chai Development Phase II and Central Wanchai Bypass involves the construction and operation of primary and district distributor roads that is shown at *Figure 2.1*.
- 2.2.2. The key purpose of the study area encompasses the Wan Chai harbourfront area. The area starts at the boundary of Central Reclamation Phase III (CRIII) at the west and connects to the existing Hung Hing Road at the east. The scope of the project includes:
 - A dual 2-lane primary distributor road, Road P2, approximately 0.6km in length; and
 - Other new primary and district distributor roads connecting to the slip roads of the Central-Wan Chai Bypass with a total length of approximately 0.7km.
- 2.2.3. The project also contains various Schedule 2 DP that, under the EIAO, require Environmental Permits (EPs) to be granted by the DEP before they may be either constructed or operated.
 Table 2.1 summarises the DP under this Project. <u>Figure 2.1</u> shows the locations of these Schedule 2 DP.

Table 2.1 Schedule 2 Designated Project under this Project

Item	Designated Project	EIAO Reference	
DP2	Road P2 and other roads which are classified as	Schedule 2, Part I, A.1	
	primary/district distributor roads		

2.2.4. The designated project work II (DP2) was awarded to China State – Build King Joint Venture HK/2012/08 (Contract Title: Wan Chai Development Phase II Central – Wan Chai Bypass at Wan Chai West) as part of the Project works by the Civil Engineering and Development Department (CEDD). The construction work under Contract no. HK/2012/08 was commenced on 13 May 2015.



2.3 Project Organization and Contact Personnel

- 2.3.1 Civil Engineering and Development Department and Highway Department are the overall project controllers for the Wan Chai Development Phase II and Central-Wan Chai Bypass respectively. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.3.2 The proposed project organization and lines of communication with respect to environmental protection works are shown in *Figure 2.2*. Key personnel and contact particulars are summarized in *Table 2.2*:

Table 2.2 Contact Details of Key Personnel

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Chief Resident Engineer	Ms. Gloria Tang	2587 1778	2587 1877
China State- Build King	Contractor under Contract	Project Director	C. N. LAI	9106 5806	2877 1522
Joint Venture	no. HK/2012/08	Site Agent	Mr. George Cheung	9268 1918	
		Environmental Officer	Mr. James Ma	9130 9549	
		Environmental Supervisor	Mr. Y.L. Ho	9856 5669	
Ramboll Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	3465 2888	3465 2899
Lam Geotechnics Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331

- 2.3.3 In this reporting month, the principal work activities of the contract is included as follows:
 <u>Contract no. HK/2012/08 Wan Chai Development Phase II Central- Wan Chai Bypass at Wan Chai West</u>
 - Landscaping
- 2.3.4 In coming reporting month, the principal work activities of the contract is anticipated as follows:

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West</u>

Landscaping



3 STATUS OF REGULATORY COMPLIANCE

3.1 Status of Environmental Licensing and Permitting under the Project

3.1.1. A summary of the current status on licences and/or permits on environmental protection pertinent to the Project is shown in *Table 3.1*.

Table 3.1 Summary of the current status on licences and/or permits on environmental protection pertinent to the Project

Permits and/or Licences	Reference No.	Issued Date	Status
Environmental Permit	EP-376/2009	13 Nov 2009	Valid
Further Environmental Permit	FEP-01/376/2009	31 Mar 2015	Valid
Further Environmental Permit	FEP-02/376/2009	1 Aug 2016	Valid

3.1.2. The current status on licences and/or permits on environmental protection pertinent for contract no. HK/2012/08 under FEP-02/376/2009 showed in *Table 3.2*. and *Table 3.3*

Table 3.2 Cumulative Summary of Valid Licences and Permits under Contract no. HK/2012/08

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-01/376/2009	31 Mar 2015	N/A	Valid
Turtier Environmental Fermit	FEP-02/376/2009	1 Aug 2016	N/A	Valid
Notification of Works Under APCO	355439	4 Feb 2013	N/A	Valid
Registration as a Chemical Waste Producer	5213-134-C3790-01	30 Jun 2016	N/A	Valid
Billing Account under Waste Disposal Ordinance	7016883	18 Feb 2013	N/A	Valid
Water Discharge Licence	WT00018470-2014	6 Mar 2014	31 Mar 2019	Expired
Construction Noise Permit	GW-RS1247-18	31 Dec 2018	13 Jan 2019 to 12 Jul 2019	Valid
Construction (voise Fermit	GW-RS0294-19	5 Apr 2019	5 Apr 2019 to 4 Oct 2019	Valid

Table 3.3 Summary of submission status under FEP-02/376/2009 Condition

EP Condition	Submission	Date of Submission
Condition 2.9	Noise Management Plan (Rev. 2)	Generally in order as commented by EPD on 27 Oct 2015
Condition 2.10	Landscape Plan (Rev. 0)	Generally in order as commented by EPD on 5 Aug 2015

3.1.3. Implementation status of the recommended mitigation measures during this reporting month is presented in *Appendix 3.1*.



4 MONITORING REQUIREMENTS

4.1 Noise Monitoring

NOISE MONITORING STATION

4.1.1. The noise monitoring station for the Project is listed and shown in *Table 4.1* and *Figure 4.1*.

**Appendix 4.1* shows the established Action/Limit Levels for the monitoring works.

Table 4.1 Noise Monitoring Station

District	Station	Description
Wan Chai	M1a	Footbridge for Ex-Harbour Road Sports Centre

NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.1.2. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (Leq). Leq (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods, Leq (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. Supplementary information for data auditing, statistical results such as L10 and L90 shall also be obtained for reference.
- 4.1.3. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
 - One set of measurements between 0700 and 1900 hours on normal weekdays.

MONITORING EQUIPMENT

- 4.1.4. As referred to in the Technical Memorandum ™ issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.
- 4.1.5. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

4.2 Air Quality Monitoring

AIR QUALITY MONITORING STATIONS

4.2.1. The air quality monitoring stations for the Project are listed and shown in *Table 4.2* and *Figure*4.1. Appendix 4.1 shows the established Action/Limit Levels for the monitoring works.

Table 4.2 Air Quality Monitoring Stations

Station ID	Description
CMA5b	Pedestrian Plaza
CMA6a	WDII PRE Site Office

AIR QUALITY MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 4.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.
- 4.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.

SAMPLING PROCEDURE AND MONITORING EQUIPMENT

- 4.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:
 - 0.6 1.7 m³ per minute adjustable flow range;
 - Equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
 - Installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
 - Capable of providing a minimum exposed area of 406 cm2;
 - Flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
 - Equipped with a shelter to protect the filter and sampler;
 - Incorporated with an electronic mass flow rate controller or other equivalent devices;
 - Equipped with a flow recorder for continuous monitoring;



- Provided with a peaked roof inlet;
- Incorporated with a manometer;
- Able to hold and seal the filter paper to the sampler housing at horizontal position;
- · Easily changeable filter; and
- Capable of operating continuously for a 24-hour period.
- 4.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

LABORATORY MEASUREMENT / ANALYSIS

- 4.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.
- 4.2.8. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.
- 4.2.9. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.
- 4.2.10. All the collected samples shall be kept in a good condition for 6 months before disposal.



5 MONITORING RESULTS

- 5.0.1. The environmental monitoring will be implemented based on the division of works areas of the designated project managed under the contract with FEP applied by individual contractors. Overall layout showing work areas of various contracts, latest status of work commencement and monitoring stations is shown in *Figure 2.1* and *Figure 4.1*.
- 5.0.2. The environment monitoring schedules for reporting month and coming month are presented in *Appendix 5.1*.

5.1 Noise Monitoring Results

5.1.1 The proposed division of noise monitoring station is summarized in *Table 5.1* below.

Table 5.1 Noise Monitoring Station for Contract no. HK/2012/08

Location ID	District	Description
M1a	Wan Chai	Footbridge for Ex-Harbour Road Sports Centre

- 5.1.2 With respect to WDII RSS confirmed that the remaining works under HK/2012/08 would be tree planting works at EP-376/2009 area only, considered that no adverse noise impact would be contributed by the tree planting works, the respective noise monitoring at noise monitoring station M1a Footbridge at EX-Wanchai Harbour Road Sports Centre was temporary suspended from 27 March 2019 onwards.
- 5.1.3 The noise monitoring results measured in the past reporting period are reviewed and summarized. Details of the noise monitoring results and graphical presentation can be referred to <u>Appendix 5.2.</u>



5.2 Air Quality Monitoring Results

5.2.1 The proposed division of air quality monitoring stations are summarized in *Table 5.2* below.

Table 5.2 Air Quality Monitoring Station for Contract no. HK/2012/08

Station	Description
CMA5b	Pedestrian Plaza
CMA6a	WDII PRE Site Office

- 5.2.2 With respect to WDII RSS confirmed that the remaining works under HK/2012/08 would be tree planting works at EP-376/2009 area only, considered that no adverse air quality impact would be contributed by the tree planting works, the respective air quality monitoring at air quality monitoring stations CMA5b Pedestrian Plaza and CMA6a Contractor HK/2012/08 Site Office were temporary suspended from 27 March 2019 onwards
- 5.2.3 The air quality monitoring results measured in the past reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in *Appendix 5.3*.

5.3 Waste Monitoring Results

5.3.1 No Inert and non-inert C&D wastes disposed in this reporting month. Details of the waste flow table are summarized in *Table 5.3*.

Table 5.3 Details of Waste Disposal for Contract no. HK/2012/08

Waste Type	Quantity this month	Cumulative Quantity- to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m3	NIL	NIL	NIL
Inert C&D materials recycled, m3	NIL	NIL	NIL
Non-inert C&D materials disposed, m3	NIL	NIL	NIL
Non-inert C&D materials recycled, m3	NIL	NIL	NIL
Chemical waste disposed, kg	NIL	NIL	NIL



6 COMPLIANCE AUDIT

6.0.1. The Event Action Plan for construction noise and air quality are presented in Appendix 6.1.

6.1 Noise Monitoring

6.1.1 With respect to WDII RSS confirmed that the remaining works under HK/2012/08 would be tree planting works at EP-376/2009 area only, considered that no adverse noise impact would be contributed by the tree planting works, the respective noise monitoring at noise monitoring station M1a - Footbridge at EX-Wanchai Harbour Road Sports Centre was temporary suspended from 27 March 2019 onwards.

6.2 Air Quality Monitoring

6.2.1 With respect to WDII RSS confirmed that the remaining works under HK/2012/08 would be tree planting works at EP-376/2009 area only, considered that no adverse air quality impact would likely be contributed by the tree planting works, the respective air quality monitoring at air quality monitoring stations CMA5b – Pedestrian Plaza and CMA6a – Contractor HK/2012/08 Site Office were temporary suspended from 27 March 2019 onwards.

6.3 Review of the Reasons for and the Implications of Non-compliance

6.3.1 There was no non-compliance from the site audits in the reporting period. The observations and recommendations made in each individual site audit session were presented in Section 8.

6.4 Summary of action taken in the event of and follow-up on non-compliance

6.4.1 There was no particular action taken since no non-compliance was recorded from the site audits in the reporting period.



7 CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS

- 7.0.1. According to the Condition 3.4 of the EP-376/2009, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) and Wan Chai Development Phase II Central Wan Chai Bypass at Wan Chai East (CWB Tunnel).
- 7.0.2. According to the Final EM&A report of Central Reclamation Phase III (CRIII) for Contract HK 12/02, the major construction activities were completed by end of January 2014 and no construction activities were undertaken thereafter and the water quality monitoring was completed in October 2011. As such, it is considered that there were no cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) undertaken by contractor HK12/02 in the reporting month.
- 7.0.3. According to the construction programme of Central-Wanchai Bypass at Wanchai West at the Central Reclamation Phase III area include roadworks, drainage, seawall coping, dismantling of temporary landing steps and junction modification were performed in June 2019 reporting period. As no project related exceedance were recorded during the reporting period, cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was considered as insignificant.
- 7.0.4. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activities under Wan Chai Development Phase II were road and drains construction and trimming work at WCR4 at Wan Chai. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were ventilation building ABWF works and junction modification at Central; seabed reinstatement at Causeway Bay; road works, drainage improvement work, utility diversion works and landscape works at Victoria Park; bridge noise enclosure installation works, road works, drainage works, soft landscape works and ventilation building ABWF work at North Point area in the reporting period. In addition, other non-Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects were observed undertaken at Wan Chai North and North Point area.



8 ENVIRONMENTAL SITE AUDIT

- 8.0.1. Five site inspections for Contract no. HK/2012/08 were carried out on 28 May, 5, 11, 18 and 25 June 2019 in this reporting period. No observation was found in the reporting period.
 - Mitigation measures implemented to prevent muddy discharge and surface runoff
- 8.0.2. In respect to EPD concern on muddy discharge and surface runoff from construction works during wet season, the following mitigation measures was implemented by Contractor(s):

Contract No.	Mitigation Measures implemented
	 Deployment of embankment along seawall Regular cleaning the sand / silt / mud sitting along the seawall Hard paved the area along seafront
HK/2012/08	 Cover the stockpile material to avoid excessive surface runoff Regular review and maintenance of the site drainage system Discharge of wastewater via wastewater treatment plant if necessary

9 COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION

- 9.0.1. No environmental complaint was received in the reporting period.
- 9.0.2. The details of cumulative complaint log and updated summary of complaints are presented in <u>Appendix 9.1</u>
- 9.0.3. Cumulative statistic on complaints and successful prosecutions are summarized in *Table 9.1* and *Table 9.2* respectively.

Table 9.1 Cumulative Statistics on Complaints

Reporting Period	No. of Complaints
Commencement works (May 2015) to last reporting month	0
June 2019	0
Total	0

Table 9.2 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative No. Project-to-Date
Air	0	0	0
Noise	0	0	0
Water	0	0	0
Waste	0	0	0
Total	0	0	0



10 CONCLUSION


- 10.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.
- 10.0.2. The scheduled construction activities and the recommended mitigation measures for the coming month are listed in *Table 10.1*. The construction programmes of individual contracts are provided in *Appendix 10.1*.

Table 10.1 Summary of Key Construction Activities of Individual Contract(s) to be commenced in Coming Reporting Month

Contract No.	Key Construction Works	Recommended Mitigation Measures
HK/2012/08	• Landscaping	• Nil

Figure 2.1

Project Layout

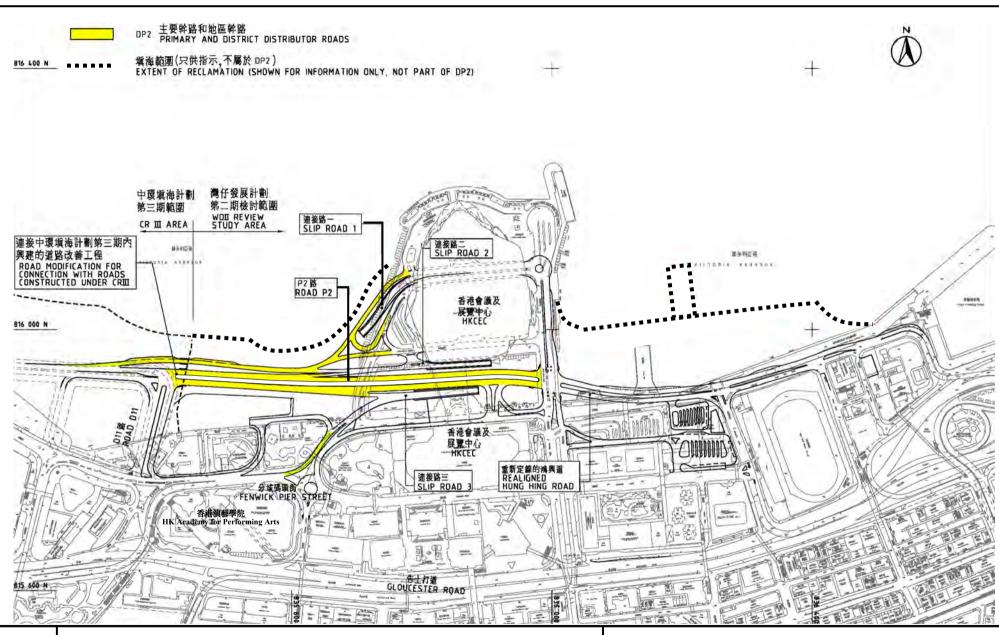



Project Title : Road P2 and other roads which are classified as primary/district distributor roads (referred to as "DP2" in the WDII&CWB EIA Report)

工程項目名稱: P2 路及其他分類爲主要幹路或地區幹路的道路(WDII&CWB 環評報告內稱 "DP2")

Environmental Permit No.: EP-376/2009 環境許可證編號 : EP-376/2009 Figure 1: Location of the Project

圖 1: 工程項目位置圖

(This figure was prepared based on Figure 1.2b of the WDII&CWB EIA report (Register No.: AEIAR-125/2008)) (本圖是根據 WDII&CWB 環評報告(登記冊編號 AEIAR-125/2008)圖 1.2b 編制)

Figure 2.2

Project Organization Chart

Project Organization Chart


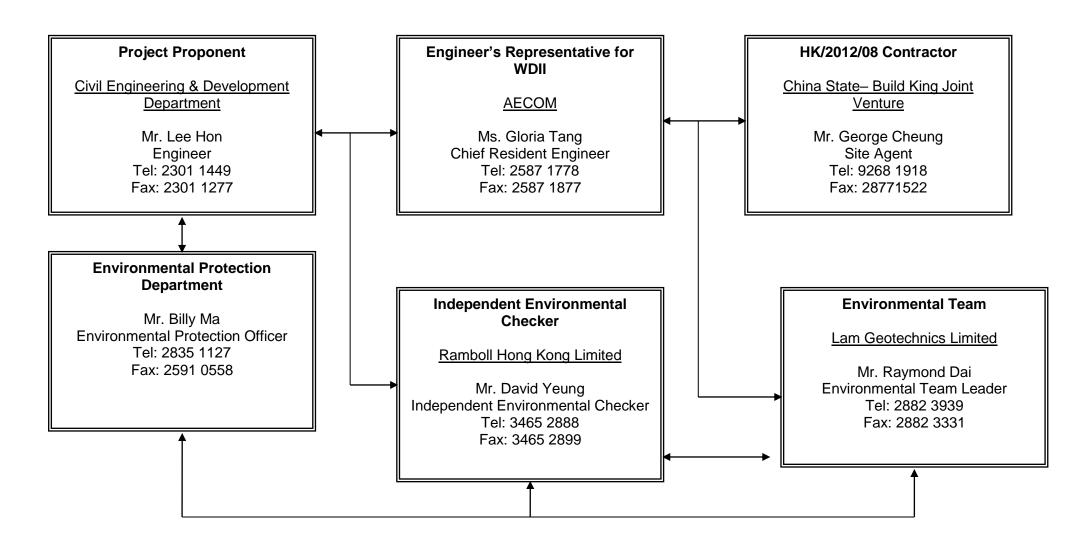


Figure 4.1

Locations of Monitoring Stations

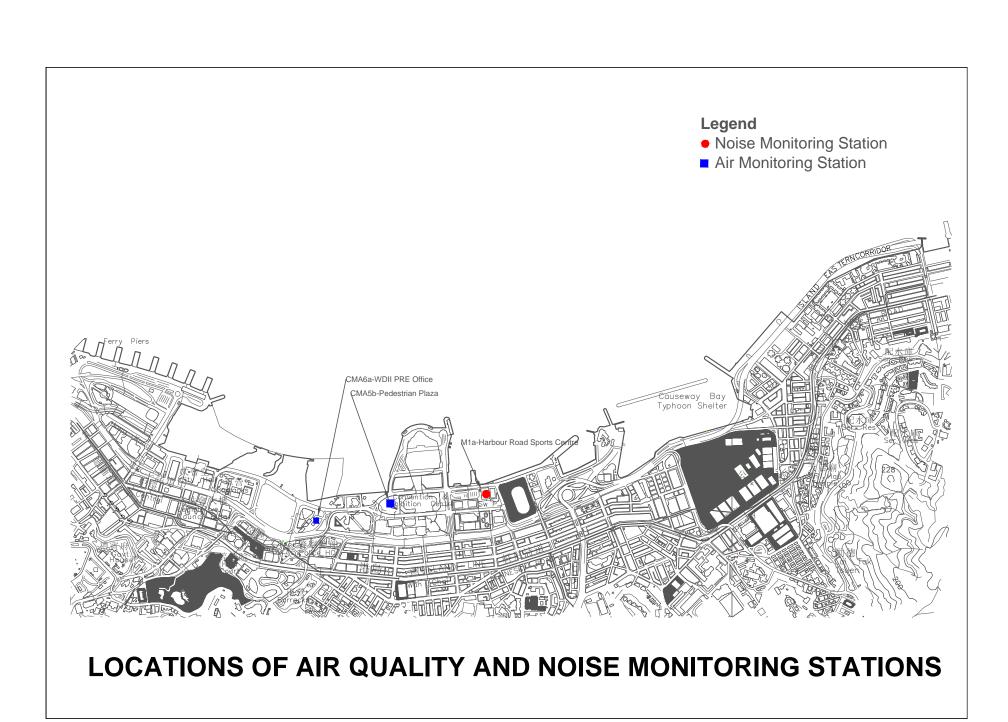

Appendix 3.1

Environmental Mitigation Implementation Schedule

Appendix A

Table A13.1 Implementation Schedule for Air Quality Control

Table A13.2 Implementation Schedule for Noise Control

Table A13.3 Implementation Schedule for Water Quality Control

Table A13.4 Implementation Schedule for Waste Management

Table A13.7 Implementation Schedule for Landscape and Visual

IMPLEMENTATION SCHEDULE OF THE PROPOSED MITIGATION MEASURES

Table A13.1 Implementation Schedule for Air Quality Control

EIA Ref	Environmental Protection Measures /	Location / Timing	Implementation	Impl	ement	ation	stage	Relevant Legislation
	Mitigation Measures		Agent	Des	C	О	Dec	and Guidelines
Constructio	n Phase							
For the Who	ole Project							
S3.6.5	Four times a day watering of the work site with active operations.	Work site / during construction	Contractor		1			EIAO-TM
S3.8.1	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimise cumulative dust impacts. Strictly limit the truck speed on site to below 10 km per hour and water spraying to keep the haul roads in wet condition; Watering during excavation and material handling; Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary; and Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.	Work site / during construction	Contractor		V			

Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Table A13.2 Implementation Schedule for Noise Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	Implementation st			stage	Relevant Legislation
			Agent	Des	C	О	Dec	and Guidelines
Constructio	n Phase		L			<u> </u>		
For the Who	ole Project							
S4.9.4	Good Site Practice: Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program. Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program. Mobile plant, if any, shall be sited as far away from NSRs as possible. Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum. Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from onsite construction activities.	Work site / during construction	Contractor		V			EIAO-TM, NCO
S4.8.3 – S4.8.4	Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the	Work site / during construction	Contractor		V			EIAO-TM, NCO
	following tasks: Temporary road diversion Resurfacing At-grade roadwork							

[•] Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

Table A13.3 Implementation Schedule for Water Quality Control

EIA Ref	Environmental Protection Measures /	Location / Timing Implementation			ement	tation s	stage	Relevant Legislation
	Mitigation Measures		Agent	Des	C	0	Dec	and Guidelines
Construction	n Phase		1			I		
For the Who	le Project							
For the Who S5.8	Construction Runoff and Drainage use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow; Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94; a sediment tank constructed from preformed individual cells of approximately 6 - 8 m3 capacity can be used for settling ground water prior to disposal; Oil interceptors shall be provided in the drainage system for the tunnels and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor shall have a bypass to prevent flushing during periods of heavy rain; precautions and actions to be taken when a rainstorm is imminent or forecast, and during or after rainstorms. Particular attention shall be paid to the control of any silty surface runoff during storm events; On-site drainage system shall be installed prior to the commencement of other	Work site / during construction	Contractor					ProPECC PN 1/94; WPCO (TM-DSS)

	installed in order to minimise the sediment loading of the effluent prior to discharge; All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge shall be adequately designed for the controlled release of storm flows. All sediment control measures shall be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage shall be reinstated to its original condition when the construction work is finished or the temporary diversion is no longer required. All fuel tanks and store areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity. Minimum distances of 100 m shall be maintained between the storm water discharges				
S5.8	and the existing or planned WSD flushing water intakes during construction phase. Sewage from Construction Work Force Construction work force sewage discharges on site shall be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage shall be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor shall also be responsible for waste disposal and maintenance practices.	Work site / during construction	Contractor	N	ProPECC PN 1/94; WPCO (TM-DSS)

<u>EP-376/2009</u> EM&A Manual

S5.8	Floating Debris and Refuse	Work site and	Contractor			WPCO
	Collection and removal of floating refuse shall	adjacent water /				
	be performed at regular intervals on a daily	During the				
	basis. The contractor shall be responsible for	construction period.				
	keeping the water within the site boundary and					
	the neighbouring water free from rubbish.					
S5.8	Storm Water Discharges	Work site and	Contractor	 		WPCO
	Minimum distances of 100 m shall be	adjacent water				
	maintained between the existing or planned	/ During the design				
	stormwater discharges and the existing or	and construction				
	planned WSD flushing water intakes.	period.				

• Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

Table A13.4 Implementation Schedule for Waste Management

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation stage				Relevant Legislation
				Des	C	О	Dec	and Guidelines
Construction	on Phase		<u>l</u>	1				<u> </u>
For the Who	ole Project							
S6.7.7	Good Site Practices Recommendations for good site practices during the construction activities include: nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; training of site personnel in proper waste management and chemical waste handling procedures; provision of sufficient waste disposal points and regular collection for disposal; appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and a recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).	Work site / During planning and design stage, and construction stage	Contractor					
S.6.7.8	Waste Reduction Measures Recommendations to achieve waste reduction include: • Sort C&D waste from demolition of the existing waterfront structures to recover	Work site / During planning and design stage, and construction stage	Contractor	V	V			

EP-376/2009 EM&A Manual

	 recyclable portions such as metals. Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal. Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force. Any unused chemicals or those with remaining functional capacity shall be recycled. Use of reusable non-timber formwork, such as in casting the tunnel box sections, to reduce the amount of C&D material. Proper storage and site practices to minimise the potential for damage or contamination of construction materials. Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. 					
S6.7.10	General Refuse General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D material. A collection area shall be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind	Work site / During the construction period	Contractor	V	Public Health and Municipal Services Ordinance (Cap. 13	

EP-376/2009 EM&A Manual

S6.7.11	Chemical Wastes After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals shall be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work site / During the construction period	Contractor	V	Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
S6.7.12 – S6.7.13	Construction and Demolition Material C&D material shall be sorted on-site into inert C&D material (that is, public fill) and C&D waste. All the suitable inert C&D material shall be broken down to 250 mm in size for reuse as public fill in the WDII reclamation. C&D waste, such as wood, glass, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials.	Work site / During the construction period	Contractor and Independent Environmental Checker	V	DEVB TCW No.6/2010; ETWB TCW No. 33/2002; ETWB TCW No. 19/2005
	In order to monitor the disposal of public fill and C&D waste at public fill reception facilities and landfills, respectively, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team undertaking the environmental monitoring and audit work. An Independent Environment Checker shall be responsible for auditing the results of the system.				
S6.7.14	Bentonite Slurry The disposal of residual used bentonite slurry shall follow the good practice guidelines stated	Work site / During the construction period	Contractor	V	ProPECC PN 1/94

EP-376/2009 EM&A Manual in ProPECC PN 1/94 "Construction Site Drainage" and listed as follows: If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis. If the used bentonite slurry is intended to be disposed of through the public drainage system, it shall be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the Technical Memorandum of Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters. If the used bentonite slurry is intended to be disposed to public fill reception facilities, it will be mixed with dry soil on site before disposal.

• Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

EP-376/2009 EM&A Manual

Table A13.7 Implementation Schedule for Landscape and Visual

EIA Ref	Environmental Protection Measures /	Location / Timing	Implementation	Imp	lemen	tation	stage	Relevant Legislation
	Mitigation Measures		Agent	Des	C	0	Dec	and Guidelines
Construction	n Phase		1		1			
For the Who	le Project							
Table 10.5	CM1 Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	V	1			EIAO TM
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	1	1			EIAO TM
Table 10.5	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	1	1			EIAO TM
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		1			EIAO TM
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		1			EIAO TM
For DP2 - V	VDII Major Roads (Road P2)							
Table 10.5	CM1 Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	√	1			EIAO TM
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	V	V			EIAO TM
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	1	√			EIAO TM
Table 10.5	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	1	√			EIAO TM
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		1			EIAO TM

EP-376/2009 EM&A Manual

Operation Pl	Operation Phase									
For DP2 – WDII Major Roads (Road P2)										
Table 10.6, Figure	OM1 Aesthetic design of buildings and road- related structures,	Work site / During Design Stage and	CEDD/HyD	V	1		ETWB TCW 2/2004			
10.5.1-	including viaducts, vent buildings, subways,	Operation Phases								
10.5.5	footbridges									
Table 10.6,	and noise barriers and enclosure. OM3 Buffer Tree and Shrub Planting to screen	Work site / During	CEDD/HyD	V	1		ETWB TCW 2/2004			
Figure	proposed roads	Design Stage and		'	'					
10.5.1-	and associated structures.	Operation Phases								
10.5.5 Table 10.6.	OM5 Aesthetic streetscape design.	Work site / During	CEDD/HyD	V	1		ETWB TCW 2/2004			
Figure		Design Stage and		'	'					
10.5.1- 10.5.5		Operation Phases								
Table 10.6,	OM6 Aesthetic design of roadside amenity areas	Work site / During	CEDD/HyD	V	1		ETWB TCW 2/2004			
Figure	22.20 22.20.000	Design Stage and			1					
10.5.1-		Operation Phases								
10.5.5										

[•] Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

Appendix 4.1

Action and Limit Level

Action and Limit Level

Action and Limit Level for Noise Monitoring

Time Period	Action Level	Limit Level
07:00 - 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A)

Notes: If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed. *The Limit level shall be 70 dB(A) and 65 dB(A) for educational institute during normal teaching periods and school examination periods, respectively.

Action and Limit Level for Air Monitoring

Monitoring Locations	1-hour TSP Level inµg/m3		24-hour TSP Level inµg/m3	
	Action Level	Limit Level	Action Level	Limit Level
CMA5b Pedestrian Plaza	339.7	500	209.9	260
CMA6a WDII PRE Site Office	333.0	500	207.1	260

Appendix 5.1

Monitoring Schedules for Reporting Month and Coming Reporting Month

Contract No. HK/2015/01 Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3)

Environmental Monitoring Schedule June 2019

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	27-May	28-May	29 - May	30-May	31-May	01-Jun
		Weekly Environmental Site Audit				
02-Jun	03-Jun	04-Jun	05-Jun	06-Jun	07-Jun	08-Jun
			Weekly Environmental Site Audit			
	40 hz	44 ha	40 ha	40 hr	44 ha	45 ha
09-Jun	10-Jun	11-Jun	12-Jun	13-Jun	14-Jun	15-Jun
		Weekly Environmental Site Audit				
16-Jun	17-Jun	18-Jun	19-Jun	20-Jun	21-Jun	22-Jun
		Weekly Environmental Site Audit				
23-Jun	24-Jun	25-Jun	26-Jun			
		Weekly Environmental Site Audit				

Contract No. HK/2015/01 Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3)

Tentative Environmental Monitoring Schedule July 2019

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		Weekly Environmental Site Audit		27-Jun	28-Jun	29-Jun
30-Jun	01-Jul	Weekly Environmental Site Audit	03-Jul	O4-Jul	05-Jul	06-Jul
07-Jul	08-Jul	09-Jul Weekly Environmental Site Audit	10-Jul	11-Jul	12-Jul	13-Jul
14-Jul	15-Jul	16-Jul Weekly Environmental Site Audit	17-Jul	18-Jul	19-Jul	20-Jul
21-Jul	22-Jul	23-Jul Weekly Environmental Site Audit	24-Jul	25-Jul	26-Jul	27-Jul


Appendix 5.2

Noise Monitoring Results and Graphical Presentations



Graphic Presentation of Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

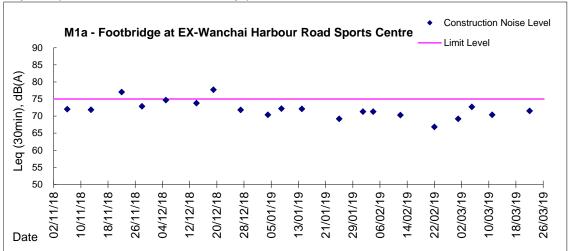


Appendix 5.3

Air Quality Monitoring Results and Graphical Presentations





Graphic Presentation of 1 hour TSP Result for EP-376/2009 1hour TSP Concentration CMA5b - Pedestrian Plaza Limit Level 600 550 TSP Concentration (µg/m3) 500 450 • 400 350 300 250 200 150 100 50 08/12/2018 02/03/2019 15/10/2018 21/10/2018 08/11/2018 14/11/2018 20/11/2018 26/11/2018 02/12/2018 14/12/2018 20/12/2018 26/12/2018 01/01/2019 07/01/2019 19/01/2019 25/01/2019 06/02/2019 12/02/2019 18/02/2019 24/02/2019 08/03/2019 14/03/2019 20/03/2019 26/03/2019 27/10/2018 02/11/2018 13/01/2019 31/01/2019 Date

Graphic Presentation of 24 hour TSP Result for EP-376/2009

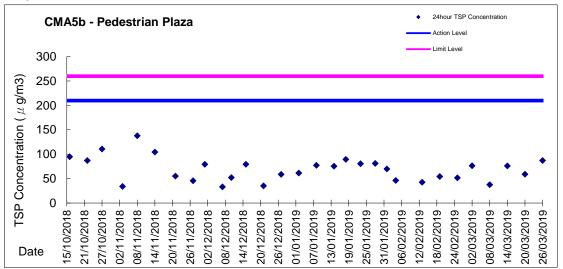



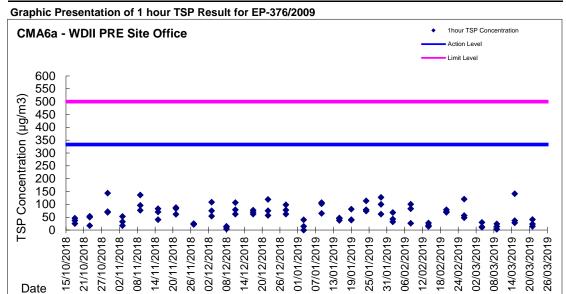

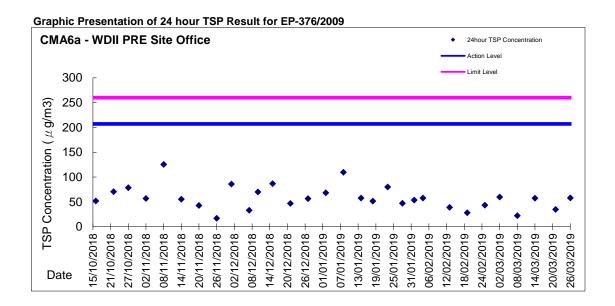

Appendix 6.1

Event Action Plans

Event/Action Plan for Construction Noise

EVENT		AC	CTION	
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	 Notify ER, IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, ER and Contractor; Discuss with the IEC and Contractor on remedial measures required; Increase monitoring frequency to check mitigation effectiveness. (The above actions should be taken within 2 working days after the exceedance is identified) 	1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Advise the ER on the effectiveness of the proposed remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	 Confirm receipt of notification of failure in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified) 	Submit noise mitigation proposals to IEC and ER; Implement noise mitigation proposals. (The above actions should be taken within 2 working days after the exceedance is identified)



EVENT		AC	CTION	
	ET	IEC	ER	CONTRACTOR
Limit Level being exceeded	 Inform IEC, ER, Contractor and EPD; Repeat measurements to confirm findings; Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contractor's working procedures; 6. Discuss with the IEC, Contractor and ER on remedial measures required; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified) 	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. (The above actions should be taken within 2 working days after the exceedance is identified)	 Confirm receipt of notification of failure in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures; If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. The above actions should be taken within 2 working days after the exceedance is identified) 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC and ER within 3 working days of notification; Implement the agreed proposals; Submit further proposal if problem still not under control; Stop the relevant portion of works as instructed by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)

Event / Action Dian for Construction Air Quality

FVENT	ACTION						
EVENT	ET	IEC	ER	CONTRACTOR			
ACTION LEVEL							
Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; Increase monitoring frequency to daily. (The above actions should be taken within 2 working days after the exceedance is identified)	Check monitoring data submitted by ET; Check Contractor's working method. (The above actions should be taken within 2 working days after the exceedance is identified)	Notify Contractor. (The above actions should be taken within 2 working days after the exceedance is identified)	Rectify any unacceptable practice; Amend working methods if appropriate (The above actions should be taken within 2 working days after the exceedance is identified)			
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Supervise Implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	Submit proposals for remedial to ER within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)			
LIMIT LEVEL							
Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. (The above actions should be taken within 2 working days after the exceedance is identified)	Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ER on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification 3. Implement the agreed proposals; Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)			
Exceedance for two or more consecutive samples	Notify IEC, ER, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring, (The above actions should be taken within 2 working days after the exceedance is identified)	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures.	Confirm receipt of notification of failure in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification 3. Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)			



Event and Action Plan for Marine Water Quality

EVENT		ACTION		
	ET	IEC	ER	CONTRACTOR
Action level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Action level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next working day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)

am	Lam Geotechnics Limited


EVENT		ACTION											
	ET	IEC	ER	CONTRACTOR									
Limit level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)									
Limit level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3working days; Implement the agreed mitigation measures; As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities. (The above actions should be taken within 1 working day after the exceedance is identified)									

Event and Action Plan for Odour Patrol

Event		ACTION
	Person-in-charge of Odour Monitoring	Implementation Agent Identified by CEDD
Action Level		
Exceedance of Action Level	Identify source/reason of exceedance; Repeat odour patrol to confirm finding.	 Carry out investigation to identify the source/reason of exceedance; Rectify any unacceptable practice Implement more mitigation measures if necessary; Inform EPD or MD if exceedance is considered to be caused by expedient connections or floating debris.
Limit Level		
Exceedance of Limit Level	I. Identify source / reason of exceedance; Repeat odour patrol to confirm findings; Increase odour patrol frequency; If exceedance stops, cease additional odour patrol.	 Carry out investigation to identify the source/reason of exceedance. Investigation shall be completed within 2 weeks; Rectify any unacceptable practice; Formulate remedial actions; Ensure remedial actions properly implemented; If exceedance continues, consider what more/enhanced mitigation measures shall be implemented; Inform EPD or MD if exceedance is considered to be caused by expedient connections or floating debris.

Appendix 6.2

Summary for Notification of Exceedance



Sampling, Field Measurement and Testing Work

Lam Geotechnics Limited

Summary for Notification of Exc

Parameters (Unit) Measured Action Level Limit Level Follow-up action



Date

Location

Ref no.

Appendix 9.1

Complaint Log

Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					ł	

Appendix 10.1

Construction Programme of Individual Contracts

	14.88.9	CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central - Wan Chai Bypass at Wan Chai West											Page : 1 / 7														
tivity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	Jan	Feb	Mar	Apr	May	Jun 20	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	2019 Jun	Jul	Aug	Sep	Oct /
	Revised Works Programme Rev.12.0(DD 20 No	ovember 2	017)																			,	- Cum	oui	Aug	Зер	Oct
	nd Milestone Dates Vorks Completion (Included Not Granted EOT Enti																										
KD10840	Completion of Section IIIA	trement or	ine Contracto		004																						
KD10860	Complection of Section IV	0		08-Sep-18*	0%									•													
KD10880	Completion of Section V	0		30-Aug-18* 26-Sep-18*	0%																						
KD11010	Completion of Section VII	0			0%									_													
KD11020	Completion of Section VIII	0		14-Sep-18* 21-Sep-18*	0%									•										•			
KD11040	Completion of Section IX	0		21-Sep-19*	0%																						
KD11060	Completion of Section X	0		21-Sep-19*	0%									_												•	
	tions of Works Completion			21 Sep 10	0 76									•													
KD10080	Planned Section IIIA Completion - Road A2,A4, A5	0		08-Sep-18	0%									_													
KD10100	Planned Section IV Completion - Slip Road 3	0		30-Aug-18	0%									•													
KD10140	Planned Section V Completion - Remaining At-Grade Road	0		26-Sep-18	0%									_													
KD10280	Planned Section VII Completion - Remainder Works	0		14-Sep-18	0%																						
KD10300	Planned Section VIII Completion - Landscape Softwork	0		21-Sep-18	0%																						
KD10320	Planned Section IX Completion - Establishment Works	0		21-Sep-19	0%																						
KD10340	Planned Section X Completion - Tree Protection & Preservation	0		21-Sep-18	0%									•												•	
Dredging and	d Reclamation																										
Marine Work	Construction																										
Zone CRIII																											
Seawall Cons	truction - Zone CRIII																										
	eawall- 2nd Stage																										
Seawalf 2 & :																											
MAR21371	Zone CRIII - seawall 2 & 12 - Backfilling remaining portion (type A, geotextile and filter)	0	19-Jan-18 A	27-Jan-18 A	100%																						
Zone D																											
	truction - Zone D																										
Seawall 10 &																											
MAR20630	Zone D - Seawall 10 & 11: Install remaining seawall block	14	20-Feb-18*	05-Mar-18	0%																						
MAR20650	Zone D - Seawall 10 & 11: Backfill Type A	7	06-Mar-18	12-Mar-18	0%																						
MAR20670	Zone D - Seawall 10 & 11: Lay geotextile and filter	7	13-Mar-18	19-Mar-18	0%																		i i		*******		
Construction	ction Completion																										
	Road A2, A4 & A5																										
	Utilities - Section 1 (L1806 - L1801)																										
ata Date: 0-Feb-18	Current Milestone Actual Work Critical Remaining Work Remaining Work Remaining Level of Effort				Up (Ref	odated f. to R	d Wo	orks I 2 as	Progr of 20	amm Febi	ne Re urary	v.12 2018	3)					2	Date 20-Feb		Revision 2	Chec	cked		Approv	ed	


Page: 2/7

vity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity %							018	100										2019				
SIIIA10279c	Sec III A - section 1 carriageway - sewerage pipe from M/H	0	02-Jan-18 A	03-Feb-18 A	Complete 100%	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	
SIIIA10279C	8C to F8B (night time): construct sewerage pipe Sec III A - section 1 carriageway - sewerage pipe Sec III A - section 1 carriageway - sewerage pipe from M/H	6	05-Feb-18 A																								
	F8B - F8A (night time)	0		26-Feb-18	0%																						
SIIIA10294	Sec III A - section 1 carriageway - sewerage pipe from M/H F8A - F8	8	17-Jan-18 A	28-Feb-18	27.27%	100000																					
SIIIA10295	Sec III A - carriageway - works prrior TTA stage 5: excavation and duct laying of TCSS and public lighting	7	18-Jan-18 A	27-Feb-18	0%																						
SIIIA10298	Sec III A - section 1 carriageway - works prrior TTA stage 5: road kerb	5	28-Feb-18	05-Mar-18	0%																						
SIIIA10301	Sec III A - section 1 carriageway - works prrior TTA stage 5: road formation	2	06-Mar-18	07-Mar-18	0%			1																			
SIIIA10302	Sec III A - section 1 carriageway - works prrior TTA stage	5	08-Mar-18	13-Mar-18	0%			•																			
SIIIA10303	5: laying asphalt Sec III A - section 1 carriageway - works prrior TTA stage	3	14-Mar-18	16-Mar-18	0%																						
SIIIA10310	5: road marking & preparation works Sec III A - section 1 carriageway - TTA stage 5:	1	17-Mar-18	17-Mar-18	0%			1																			
SIIIA10310a	Implementation of TTA Stage 5 Sec III A - section 1 carriageway - TTA stage 5: remaining	12	19-Mar-18	04-Apr-18	0%																						
SIIIA10310b	sewerage pipe for M/H F8A - M/H F8 Sec III A - section 1 carriageway - TTA stage 5: remaining	18	06-Apr-18	26-Apr-18	0%																					į	
SIIIA10310c	sewerage pipe for M/H F8A - M/H F8B Sec III A - section 1 carriageway - TTA stage 5: SR1	5	19-Mar-18	23-Mar-18	0%																						
SIIIA10310d	at-grade road- remove sheetpile at U-trough west	21	24-Mar-18	21-Apr-18	0%																						
	at-grade road -remove temp. road access bay 5 of SR1																										
SIIIA10310e	at-grade road -construct upstand wall above Dwall	25	23-Apr-18	23-May-18	0%				-																		
SIIIA10310f	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - roadside barrier	14	24-May-18	08-Jun-18	0%																						
SIIIA10310g	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - road formation	7	09-Jun-18	16-Jun-18	0%						-																
SIIIA10310h	Sec III A - section 1 carriageway - TTA stage 5: SR1 at-grade road - laying asphalt with transition slab	14	19-Jun-18	05-Jul-18	0%																						
SIIIA10312	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L2202 - L2201)	15	19-Mar-18	09-Apr-18	0%																						
SIIIA10312a	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (L1805 - L1801)	15	10-Apr-18	26-Apr-18	0%																						
SIIIA10312b	Sec III A - roadwork and utilities section 1 carriageway -	12	27-Apr-18	11-May-18	0%																						
SIIIA10313	Drainage works (L1805-1807) Sec III A - roadwork and utilities section 1 carriageway -	14	07-May-18	23-May-18	0%			-							<u> </u>												
SIIIA10320	gully pipe (L1807 - L1801) Sec III A - roadwork and utilities section 1 carriageway -	7	24-May-18	31-May-18	0%																						
SIIIA10340	fresh watermain Sec III A - roadwork and utities section 1 carriageway -	14	01-Jun-18	16-Jun-18	0%	1																					
SIIIA10360	utilities: HEC (80m) along carriageway Sec III A - roadwork and utilities section 1 carriageway -	14	19-Jun-18	05-Jul-18	0%																						
SIIIA10400	road kerb & formation Sec III A - roadwork and utilities section 1 carriageway -	7	06-Jul-18	13-Jul-18	0%																						
SIIIA10420	black top Sec III A - Implementation of TTA Stage 7P (Closure of	1	14-Jul-18	14-Jul-18	0%																						
	U-turn at Expo Drive)	10																									
SIIIA10440	Sec III A - roadwork and utitites section 1 carriageway : breaking existing asphalt	10	16-Jul-18	26-Jul-18	0%																						
SIIIA10460	Sec III A - roadwork and utilities section 1 carriageway: road kerb and formation	14	27-Jul-18	11-Aug-18	0%							_															
SIIIA10480	Sec III A - roadwork and utilities section 1 carriageway : black top	10	13-Aug-18	23-Aug-18	0%																						
SIIIA10500	Sec III A - roadwork and utilities section 1 carriageway : roadmarking and road furniture	14	24-Aug-18	08-Sep-18	0%																						
Roadwork &	Utilities - Section 2 (L1810 - L1807)																										
SIIIA12590	Sec III A - roadwork and utilities section 2 carriageway - black top	0	20-Jan-18 A	27-Jan-18 A	100%																						
Roadwork &	Utilities - Section 3 (L1808 - L1102)																										
SIIIA12770	Sec III A - roadwork and utilities section 3 carriageway -	0	20-Jan-18 A	07-Feb-18 A	100%		-																				
SIIIA12790	utilities: HEC ducting (60m) & crossroad duct (PCCW & HGC) Sec III A - roadwork and utilities section 3 carriageway -	17	08-Feb-18 A	10-Mar-18	0%			<u>:</u>																			
SIIIA12810	road kerb & formation Sec III A - roadwork and utilities section 3 carriageway -	7	12-Mar-18	19-Mar-18	0%																						
	black top Utilities - Section 6 (L1102 - L1411)																		-								
		0	12.lan 10 t	26-lan 10 A	10004																						
SIIIA13399	Sec III A - roadwork and utilities section 6 carriageway - gully pipe (L1101 -L1102)	0	12-Jan-18 A	26-Jan-18 A	100%																						
SIIIA13444	Sec III A - roadwork and utilities section 6 carriageway - watermain (road crossing)	0	27-Jan-18 A	03-Feb-18 A	100%																						
SIIIA13445	Sec III A - roadwork and utilities section 6 carriageway - utilities: crossed duct(HEC , HGC, PCCW)	13	05-Feb-18 A	06-Mar-18	0%																						

Page: 3 / 7

ity ID	LA objeth Alarma	Domeining Dur	Fach Start		1 1-5-2-0/	
ity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete	2018
SIIIA13450	Sec III A - roadwork and utilities section 6 carriageway - road kerb & formation	18	07-Mar-18	27-Mar-18	0%	
SIIIA13470	Sec III A - roadwork and utilities section 6 carriageway - black top	7	28-Mar-18	09-Apr-18	0%	
SIIIA13570	Achievement of Section IIIA of the Works	0		08-Sep-18	0%	
Section V - Re	emaining At-Grade Road & Road P2					
Roadwork &	Utilities					
Section 1 (L1	504 - L1900)					
SV12456	Sec V-Roadwork & Utilities Section 1 - implementation of	0	20-Feb-18*	20-Feb-18	0%	
SV12460	TTA stage 5E (closure of slow lane at northbound of Expo Sec V - Roadwork & Utilities Section 1 - drinage works	15	20-Feb-18	08-Mar-18	0%	
SV12462	(L1902 - L1900) Sec V - Roadwork & Utilities Section 1 - gully pipe (L1902 -	6	09-Mar-18	15-Mar-18	0%	
SV12464	L1900) Sec V - Roadwork & Utilities Section 1 - temp. reinstatement	14	16-Mar-18	04-Apr-18	0%	
SV12466	to match with existing Expo Drive Sec V - Section 1 - Modification to 2nd stage ITA (V.O. 50) :	1	14-Jul-18	14-Jul-18	0%	
SV12468	closure of northbound and maintain one lane at southbound Sec V - Roadwork & Utilities Section 1 Carriageway -	7	16-Jul-18	23-Jul-18	0%	
SV12490	breaking existing asphalt Sec V - Roadwork & Utilities Section 1 Carriageway - Road	10	24-Jul-18	03-Aug-18	0%	
SV12520	kerb & formation Sec V - Roadwork & Utilities Section 1 Carriageway - Black	7	04-Aug-18	11-Aug-18	0%	
SV12522	Sec V - Section 1 - Implementation of TTA for road closure	3	13-Aug-18	15-Aug-18	0%	
SV12524	of northbound and southbound of Expo Drive Sec V - Section 1 - Northbound & Southbound of Expo Drive :	14	16-Aug-18	31-Aug-18	0%	
SV12526	breaking asphalt Sec V - Section 1 - Northbound & Southbound of Expo Drive:	14	01-Sep-18	17-Sep-18	0%	
SV12528	road kerb & formation Sec V - Section 1 - Northbound & Southbound of Expo Drive : black top	7	18-Sep-18	26-Sep-18	0%	
SV12570	Sec V - Roadwork & Utilities Section 1 footpath - utilities:TCSS	12	29-Dec-17 A	05-Mar-18	60%	
SV12580	Sec V - Roadwork & Utilities Section 1 footpath - paving block	29	06-Mar-18	12-Apr-18	0%	
Section 2 (L:	1510 - L1504)					
SV12624	Sec V - Roadwork & Utilities Section 1 Carriageway - road kerb & formation	0	04-Jan-18 A	30-Jan-18 A	100%	
SV12626	Sec V - Roadwork & Utilities Section 1 Carriageway - black top	13	31-Jan-18 A	06-Mar-18	0%	
SV12692	Sec V - Roadwork & Utilities Section 2 footpath - U channel	11	17-Jan-18 A	03-Mar-18	21.43%	
SV12695	Sec V - Roadwork & Utilities Section 2 footpath - Watermain	13	05-Mar-18	19-Mar-18	0%	
SV12700	Sec V - Roadwork & Utilities Section 2 footpath - utilities: TCSS	16	20-Mar-18	11-Apr-18	0%	
SV12740	Sec V - Roadwork & Utilities Section 2 footpath - paving block	18	12-Apr-18	03-May-18	0%	
Section 3 (C	ulvert L - L1510)					
SIV12860	Sec V - Roadwork & Utilities Section 3 footpath - Utilities: TCSS, HGC, PCCW)	30	16-Jan-18 A	26-Mar-18	11.76%	
SIV12880	Sec V - Roadwork & Utilities Section 3 footpath - Paving block	21	27-Mar-18	24-Apr-18	0%	
Section 4 (K1	L106 - Culvert L)					
SIV12282	Sec V - Roadwork & Utilities Section 4 Carriageway - Drainage Works (L1311 - Culvert L, L1201 - Culvert L)	10	20-Feb-18	02-Mar-18	0%	
SIV12300	Sec V - Roadwork & Utilities Section 4 Carriageway - Gully pipe (L1301 - Culvert L, L1201 - Culvert L)	7	03-Mar-18	10-Mar-18	0%	
SIV12302	Sec V - Roadwork & Utilities Section 4 Carriageway - watermain	6	12-Mar-18	17-Mar-18	0%	
SIV12305	Sec V - Roadwork & Utilities Section 4 Carriageway - utilities : cross road duct	7	19-Mar-18	26-Mar-18	0%	
SIV12310	Sec V - Roadwork & Utilities Section 4 Carriageway - Road kerb & formation : between culvert K and culvert L	15	27-Mar-18	17-Apr-18	0%	
SIV12320	Sec V - Roadwork & Utilities Section 4 Carriageway - Black top : between culvert K and culvert L	10	18-Apr-18	28-Apr-18	0%	
SIV12340	Sec V - Roadwork & Utilities Section 4 Carriageway - Black top : at west of culvert K	7	20-Feb-18	27-Feb-18	0%	
SIV12422	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : TCSS	20	20-Feb-18	14-Mar-18	0%	
SIV12440	Sec V - Roadwork & Utilities Section 4 footpath - Utilities : HGC & PCCW	8	15-Mar-18	23-Mar-18	0%	


Page: 4 / 7

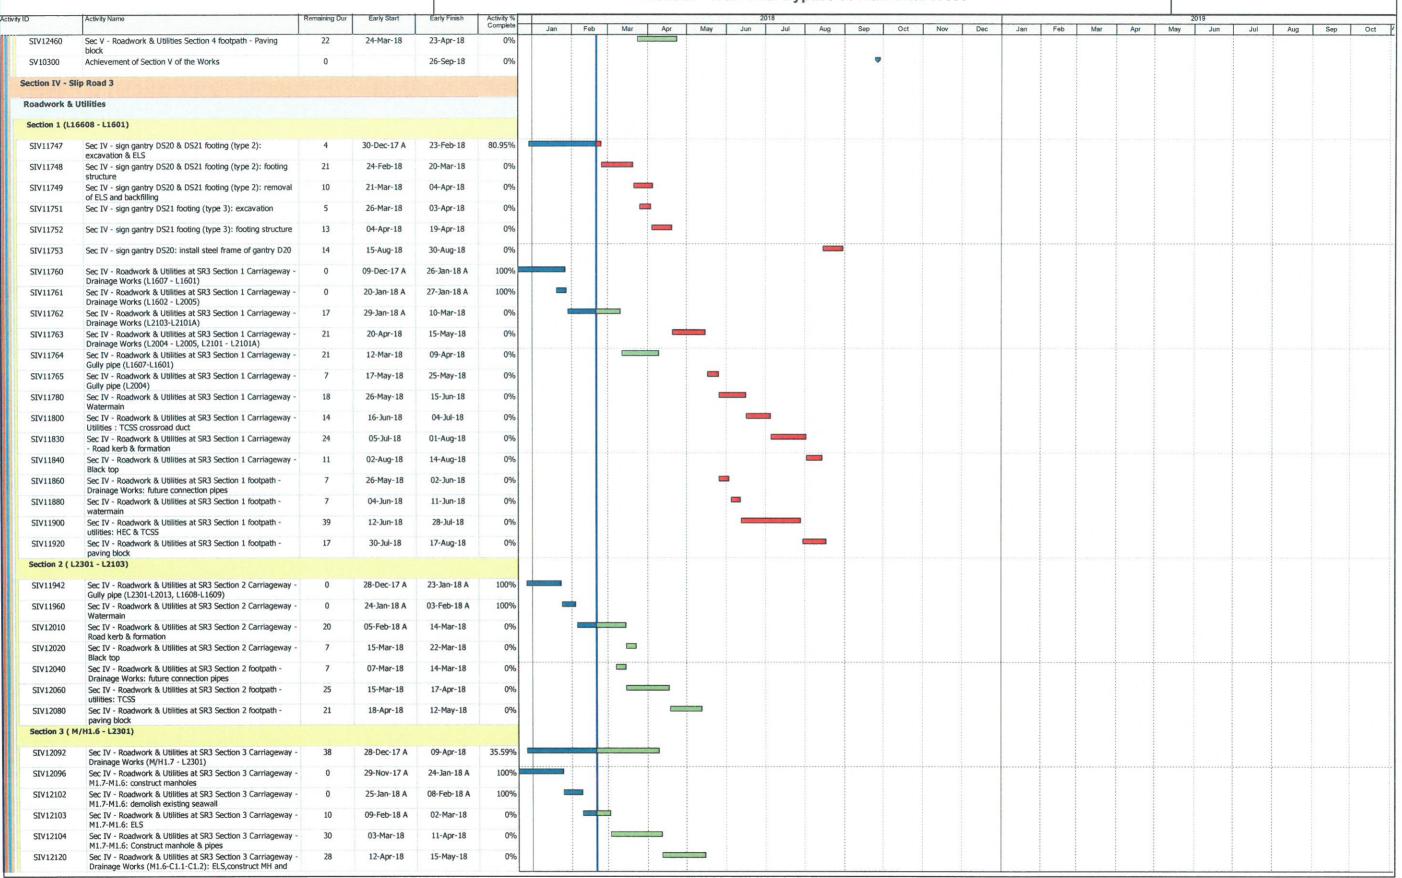

Page	:5/7	

vity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Activity % Complete							2018		2007									2019				
	Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	6	16-May-18	23-May-18	O%	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	_	Jun	Jul	Aug	Sep	Oct
	Drainage Works (M1.6-C1.1-C1.2): Backfilling & shift lane Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	5	24-May-18	29-May-18	0%						1																
SIV12140	Drainage Works (M1.6-C1.1-C1.2): Construct MH C1.2 Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	32	10-Apr-18	17-May-18	0%																						
	Gully pipe (M/H 1.7 - L2301) Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	14	18-May-18	04-Jun-18	0%																						
	Road kerb Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	10	05-Jun-18	15-Jun-18	0%																						
	formation Sec IV - Roadwork & Utilities at SR3 Section 3 Carriageway -	7	16-Jun-18	25-Jun-18	0%																						
	Black top Sec IV - Roadwork & Utilities at SR3 Section 3 footpath -	21									1																
	Utilities: TCSS	21	10-May-18	04-Jun-18	0%																						
	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - U channel	10	05-Jun-18	15-Jun-18	0%																						
	Sec IV - Roadwork & Utilities at SR3 Section 3 footpath - Paving block	25	16-Jun-18	17-Jul-18	0%																						
SIV12222	Achievement of Section IV of the Works	0		30-Aug-18	0%								•														
Section VII - Re	mainder Works					1																		÷	·	ļ	
Road & Draina	ge Works (Culvert L - M/H1.7, Adjacent to SR3)																										
	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway - Drainage Works (Culvert L -MH1.7)	48	08-Jan-18 A	20-Apr-18	18.64%																						
SVII11620	Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway :	3	21-Apr-18	24-Apr-18	0%															1 4 4 6 6							
SVII11640	traffic diversion at Lung King Street Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	27	25-Apr-18	28-May-18	0%																	1 0 0 0 1					
SVII11650	Gully pipe (Culvert L -MH1.7) Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	7	29-May-18	05-Jun-18	0%					1											ļ						
SVII11654	TCSS duct Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	14	06-Jun-18	22-Jun-18	0%																						
SVII11660	road kerb & formation Sec IV - Roadwork & Utilities at SR3 Section 4 Carriageway -	6	23-Jun-18	29-Jun-18	0%																						
	Black top Sec IV - Roadwork & Utilities at SR3 Section 4 footpath - U	14	29-May-18	13-Jun-18	0%																						
	channel Sec IV - Roadwork & Utilities at SR3 Section 4 footpath -	14	14-Jun-18	30-Jun-18	0%																						
	utilities: TCSS Sec IV - Roadwork & Utilities at SR3 Section 4 footpath -	14	03-Jul-18	18-Jul-18	0%																						
	paving block RW5 Construction			10 30 10	0.0																						
	Sec VII - Retaining Wall RW5 (bay 1) - construct base slab	22	20-Mar-18	10 4 10	000																						
	and wall Sec VII - Retaining wall RW5 (bay 2) - construct base slab			18-Apr-18	0%																						
	and wall	22	19-Apr-18	15-May-18	0%																						
	Sec VII - Retaining wall RW5 (bay 3) - construct base slab and wall	22	20-Mar-18	18-Apr-18	0%																						
	Sec VII - Retaining wall RW5 (bay 4) - construct base slab and wall	22	19-Apr-18	15-May-18	0%																						
SVII10860	Sec VII - Retaining wall RW5 - curing, removal formwork	8	16-May-18	25-May-18	0%																						
Landing Steps (Construction																										
Landing Steps	BSW13																										
	Sec VII - Landing steps (BSW13) - install vertical fender / step fender	15	15-May-18	01-Jun-18	0%						1																
	Sec VII - Landing steps (BSW13) - install s.s. handrail / tactile / sign board / bollard	25	02-Jun-18	03-Jul-18	0%	1						1											į į				
Landing Steps																											
SVII10980	Sec VII - Landing steps (BSW4) - install vertical fender / step fender	15	20-Jun-18	07-Jul-18	0%							-															
	Sec VII - Landing steps (BSW4) - install s.s. handrail / tactile	25	09-Jul-18	06-Aug-18	0%								-														
Landing Steps	/ sign board / bollard BSW5																										
SVII11060	Sec VII - Landing steps (BSW5) - install vertical fender / step	15	25-Jul-18	10-Aug-18	0%	ļ																			ļ		
	fender Sec VII - Landing steps (BSW5) - install s.s. handrail / tactile	25	11-Aug-18	08-Sep-18	0%																						
	/ sign board / bollard			- 50p 40	0,70																						
	Sec VII - Landing steps (BSW9) - install vertical fender / step	15	13-Jun-18	30-Jun-18	0%																						
	fender																										
	Sec VII - Landing steps (BSW9) - install s.s. handrail / tactile / sign board / bollard	25	03-Jul-18	31-Jul-18	0%																						

Page		6	1	7	
------	--	---	---	---	--

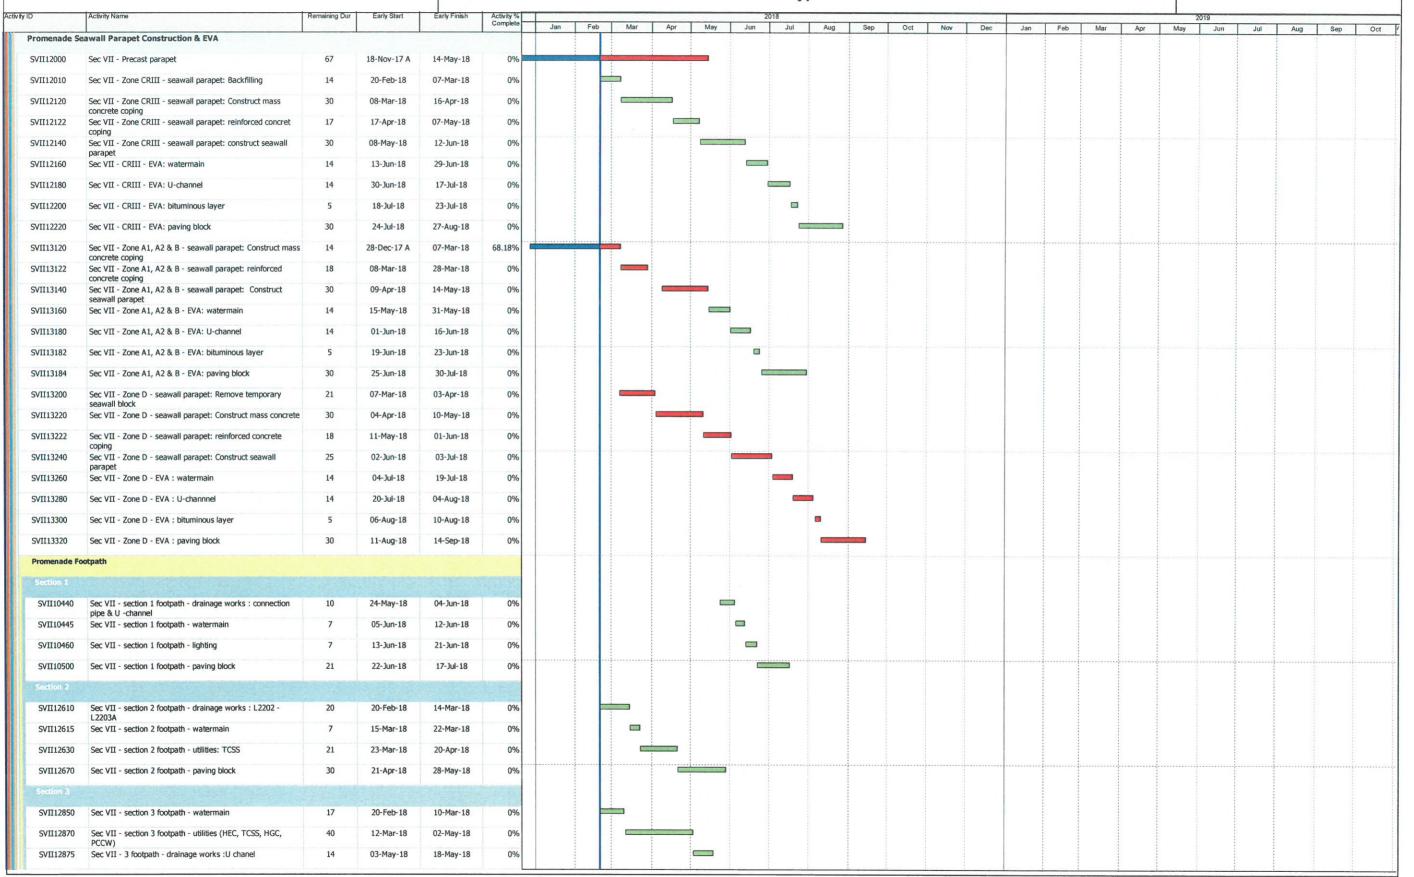

Page: 7/7

