



Lam Geotechnics Limited

Contract No. HK/2011/07
Wanchai Development Phase II and Central Wanchai Bypass
(Shatin to Central Link (SCL) Protection
Works at Causeway Bay Typhoon Shelter)
Quarterly EM&A Report (December 2013-February 2014)

CONTRACT NO: HK/2011/07

**WANCHAI DEVELOPMENT PHASE II AND CENTRAL
WANCHAI BYPASS
SAMPLING, FIELD MEASUREMENT AND TESTING WORK
(STAGE 2)**

**ENVIRONMENTAL PERMIT NO. EP- 416/2011 AND FEP-
01/416/2011**

**SHATIN TO CENTRAL LINK (SCL) PROTECTION WORKS AT
CAUSEWAY BAY TYPHOON SHELTER (CBTS)**

**QUARTERLY ENVIRONMENTAL MONITORING
AND AUDIT REPORT**

- DECEMBER 2013 TO FEBRUARY 2014 -

CLIENTS:

**Civil Engineering and Development
Department**

and

Highways Department

PREPARED BY:

Lam Geotechnics Limited

11/F Centre Point
181-185 Gloucester Road,
Wanchai, H.K.

Telephone: (852) 2882-3939
Facsimile: (852) 2882-3331
E-mail: info@lamenviro.com
Website: <http://www.lamenviro.com>

CHECKED BY:

Raymond Dai
Environmental Team Leader

DATE:

24 March 2014

24 March 2014

Ref.: AACWBIECEM00_0_5057L.14

By Post and Fax (2691 2649)

AECOM Asia Company Limited
11/F, Tower 2
Grand Central Plaza
138 Shatin Rural Committee Road
Shatin, New Territories
Hong Kong

Attention: Mr. Conrad NG

Dear Sir,

Re: Shatin to Central Link – Protection Works at Causeway Bay Typhoon Shelter
Quarterly EM&A Report (December 2013 to February 2014) for
EP-416/2011 & FEP-01/416/2011

Reference is made to the Environmental Team's submission of the captioned Quarterly Environmental Monitoring and Audit (EM&A) Report for December 2013 to February 2014 received by e-mail on 24 March 2014.

Please be informed that we have no adverse comment on the captioned submission and thereby write to verify the captioned submission.

Thank you very much for your kind attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,



David Yeung
Independent Environmental Checker

c.c.	HyD	Mr. Cyrus Wong	by fax: 2761 1508
	HyD	Mr. Jones Lai	by fax: 2714 5289
	CEDD	Mr. Patrick Keung	by fax: 2577 5040
	AECOM	Mr. Peter Poon	by fax: 3912 3010
	AECOM	Mr. Frankie Fan	by fax: 2587 1877
	MTRCL	Mr. Richard Kwan	by fax: 2993 7577
	Lam	Mr. Raymond Dai	by fax: 2882 3331

Q:\Projects\AACWBIECEM00\Corr\AACWBIECEM00_0_5057L.14.doc

TABLE OF CONTENTS

EXECUTIVE SUMMARY.....	3
1. INTRODUCTION	4
1.1 Scope of the Report	4
1.2 Structure of the Report	4
2. PROJECT BACKGROUND	5
2.1 Background	5
2.2 Scope of the Project and Site Description	5
2.3 Project Organization and Contact Personnel	6
2.4 Principle Work and Activities	7
3. MONITORING REQUIREMENTS.....	8
3.1. Noise Monitoring	8
3.2. Air Monitoring	9
3.3. Water Quality Monitoring	10
4. MONITORING RESULTS	14
4.1. Noise Monitoring Results	14
4.2. Air Monitoring Results	14
4.3. Water Monitoring Results	14
4.4. Waste Monitoring Results	15
5. COMPLIANCE AUDIT.....	17
5.1. Noise Monitoring	17
5.2. Air Monitoring	17
5.3. Water Quality Monitoring	17
5.4. Site Audit	17
6. COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION.....	18
7. CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS.....	19
8. CONCLUSION	19

LIST OF TABLES

Table 1	<i>Principle Work Activities for this reporting period</i>
Table 2.1	<i>Schedule 2 Designated Projects under this Project</i>
Table 2.2	<i>Contact Details of Key Personnel</i>
Table 2.3	<i>Principle Work Activities for this reporting period</i>
Table 3.1	<i>Noise Monitoring Stations</i>
Table 3.2	<i>Air Monitoring Stations</i>
Table 3.3	<i>Marine Water Quality Stations for Water Quality Monitoring</i>
Table 3.4	<i>Marine Water Quality Monitoring Frequency and Parameters</i>
Table 4.1	<i>Noise Monitoring Stations</i>
Table 4.2	<i>Air Monitoring Stations</i>
Table 4.3	<i>Water Monitoring Station</i>
Table 4.4	<i>Details of Waste Disposal</i>
Table 6.1	<i>Cumulative Statistics on Complaints</i>
Table 6.2	<i>Cumulative Statistics on Successful Prosecutions</i>

LIST OF FIGURES

Figure 2.1	Project Layout
Figure 2.2	Project Organization Chart
Figure 3.1	Locations of Environmental Monitoring Stations

LIST OF APPENDICES

Appendix 2.1	Environmental Mitigation Implementation Schedule
Appendix 3.1	Action and Limit Level
Appendix 4.1	Noise Monitoring Graphical Presentations
Appendix 4.2	Air Quality Monitoring Graphical Presentations
Appendix 4.3	Water Quality Monitoring Graphical Presentations
Appendix 5.1	Event Action Plans
Appendix 6.1	Complaint Log
Appendix 6.2	Notification of Exceedances
Appendix 7.1	Construction Programme of Individual Contracts

EXECUTIVE SUMMARY

- i. This is the Quarterly Environmental Monitoring and Audit (EM&A) Report – December 2013 to February 2014 prepared for the Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter (CBTS) under Environmental Permit no. EP-416/2011 and Further Environmental Permit no. FEP-01/416/2011. This report presents the environmental monitoring and audit findings and information during the period from December 2013 to February 2014. The cut-off date of reporting is at 27th of each reporting period.

Construction Activities for the Reported Period

- ii. During this reporting period, the principle work activities are summarized as below:

Table I Principle Work Activities for this reporting period

December 2013	January 2014	February 2014
<ul style="list-style-type: none"> Tunnel construction works at ME4. 	<ul style="list-style-type: none"> Dismantling of struts at ME4. Tunnel construction works at ME4. 	<ul style="list-style-type: none"> Dismantling of struts at ME4. Tunnel construction works at ME4.

Noise Monitoring

- iii. Noise monitoring during daytime was conducted at M2b - Noon-day gun area on a weekly basis. No action and limit level exceedance was recorded in the reporting quarter.

Air Quality Monitoring

- iv. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted at CMA3a - CWB PRE Site Office Area. No action or limit level exceedances were recorded in the reporting quarter.

Water Quality Monitoring

- v. Water quality monitoring at C7 was conducted three days per week during the reporting period.
- vi. Two limit level turbidity exceedances and two limit level suspended solid exceedances were recorded at C7 in this December 2013 reporting month. The exceedances were considered as works-related.
- vii. No exceedance was recorded in the January and February 2014 reporting period.

Complaints, Notifications of Summons and Successful Prosecutions

- viii. There was no environmental complaint recorded in the reporting period.

1. INTRODUCTION

1.1 Scope of the Report

- 1.1.1. Lam Geotechnics Limited (LGL) has been appointed to work as the Environmental Team (ET) under Environmental Permit no. EP-416/2011 and Further Environmental permit nos. FEP-01/416/2011 to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter (CBTS) (Register No.: AEIAR-159/2011) and in the EM&A Manual of the approved EIA Report for Shatin to Central Link Protection Works at Causeway Bay Typhoon Shelter (Register No. AEIAR-159/2011).
- 1.1.2. This report presents the environmental monitoring and auditing work carried out in accordance to the Section 7.5 of EM&A Manual and Environmental Monitoring and Audit Requirements of Environmental permit nos. EP-416/2011 and Further Environmental permit nos. FEP-01/416/2011.
- 1.1.3.** This report documents the finding of EM&A works during the period from [December 2013 to February 2014](#).

1.2 Structure of the Report

- Section 1** ***Introduction*** – details the scope and structure of the report.
- Section 2** ***Project Background*** – summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.
- Section 3** ***Monitoring Requirements*** – summarizes all monitoring parameters, monitoring locations, monitoring frequency, duration and action plan.
- Section 4** ***Monitoring Results*** – summarizes the monitoring results obtained in the reporting period.
- Section 5** ***Compliance Audit*** – summarizes the auditing of monitoring results, all exceedances environmental parameters.
- Section 6** ***Complaints, Notification of summons and Prosecution*** – summarizes the cumulative statistics on complaints, notification of summons and prosecution
- Section 7** ***Cumulative Construction Impact due to the Concurrent Projects*** – summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.
- Section 8** ***Conclusion***

2. PROJECT BACKGROUND

2.1 Background

- 2.1.1. The “Shatin to Central Link Protection Works at Causeway Bay Typhoon Shelter” (hereafter called “the Project”) is a Designed Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Reports for Shatin to Central Link Protection Works at CBTS (Register No. AEIAR-159/2011) has been approved on 25 Feb 2011.
- 2.1.2. The key purpose of the SCL Protection Works and associated works at CBTS involves the construction of a 160m tunnel box by cut-and-cover method at the crossing above the Central – Wan Chai Bypass (CWB) tunnels. Temporary reclamation is required and has been authorized under the Foreshore and Sea-bed (reclamations) Ordinance. With the presence of the Protection Works, future construction of the SCL on both sides of the CWB tunnels is protected and ensured feasible without damaging or unduly affecting the CWB tunnels which could be operational by then. This arrangement will also minimize public nuisance and impact to the surrounding environment as it can reduce the reclamation area for subsequent construction of the SCL after CWB is completed. Nevertheless, the Protection Works cannot serve to function for any railway service or operation before the completion of SCL.
- 2.1.3. The SCL is strategically important for connecting the existing railway lines into an integrated rail network. The east-west connection will allow the set up of a 57km East-West Corridor across the city connecting Wu Kai Sha with Tuen Mun via Kowloon; whilst the north-south connection will operate over a 41km North-South Corridor with services originating in Lok Ma Chau or Lo Wu travelling via the existing East Rail Line (EAL) to Admiralty. This will enable a direct transportation linkage between Mainland China and Hong Kong Island.

2.2 Scope of the Project and Site Description

- 2.2.1. The study area encompasses existing developments in Causeway Bay Typhoon Shelter as shown in **Figure 2.1**. The scope of the Project includes:
- Temporary reclamation, which occupies about 0.7ha of Government foreshore and sea-bed (of which 0.3ha is already authorized under CWB project, i.e. additional reclamation of 0.4ha is required).
 - Dredging works at the southeast corner of the CBTS to provide space for temporary relocation of anchorage area due to the additional temporary reclamation for the Project.
 - Construction of a section of the twin track railway tunnel structure (approximately 160m long) above the proposed CWB located entirely offshore within the CBTS.
 - Relocation of the temporary Royal Hong Kong Yacht Club (RHKYC) jetty within the CWB temporary reclamation to a new location.
 - Removal of the temporary reclamation, except the small area at the southwest corner of the reclamation (which will be removed by the SCL project upon completion of

the future SCL tunnels connecting to the proposed South Ventilation Building (SOV)).

- 2.2.2. The Project contains Schedule 2 DP that, under the EIAO, requires Environmental Permits (EPs) to be granted by the DEP before they may either be constructed or operated. **Table 2.1** summarises the DP under this Project. **Figure 2.1** shows the location of this Schedule 2 DPs.

Table 2.1 Schedule 2 Designated Projects under this Project

Item	Designated Project	EIAO Reference	Reason for inclusion
DP1	Temporary reclamation, which occupies about 0.7ha of Government foreshore and sea-bed	Schedule 2, Part I, C.12	A dredging operation which is less than 100m from a seawater intake point

2.3 Project Organization and Contact Personnel

- 2.3.1 Civil Engineering and Development Department and Highways Department are the overall project controllers for the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.3.2 The proposed project organization and lines of communication with respect to environmental protection works are shown in **Figure 2.2**. Key personnel and contact particulars are summarized in **Table 2.2**:

Table 2.2 Contact Details of Key Personnel

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Principal Resident Engineer	Mr. Frankie Fan	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3912 3388	3912 3010
MTR Corporation Limited	Permit Holder	Environment Manager	Mr. Richard Kwan	2688 1179	2993 7577
		Environmental Engineer I	Miss. Viola Tong	3127 6296	
		Environmental Engineer II	Mr. Chris Mak	3127 6297	
China State Construction Engineering (HK) Ltd.	Contractor under Contract no. HY/2009/15	Project Director	Mr. K C Cheung	3557 6399	2566 2192
		Site Manager	Mr. J H Chen	3557 6368	2566 2192
		Contractor's Representative	Mr. Andrew Wong	3557 6407	
		Head of construction	Mr. Roger Cheung	3557 6371	
		Environmental Officer	Mr. Andy Mak	3557 6347	
ENVIRON Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	3465 2888	3465 2899
Lam Geotechnics Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331

2.4 Principle Work and Activities

2.4.1 During this reporting period, the principle work activities for Contract no. HY/2009/15 are summarized in **Table 2.3**.

Table 2.3 Principle Work Activities for this reporting period

December 2013	January 2014	February 2014
<ul style="list-style-type: none"> Tunnel construction works at ME4 	<ul style="list-style-type: none"> Dismantling of struts at ME4. Tunnel construction works at ME4. 	<ul style="list-style-type: none"> Dismantling of struts at ME4. Tunnel construction works at ME4.

2.4.2 Implementation status of the recommended mitigation measures during this reporting period is presented in **Appendix 2.1**.

3. MONITORING REQUIREMENTS

3.1. Noise Monitoring

NOISE MONITORING STATIONS

- 3.1.1. The noise monitoring stations for the Project are listed and shown in **Table 3.1** and **Figure 3.1**. **Appendix 3.1** shows the established Action/Limit Levels for the monitoring works.

Table 3.1 Noise Monitoring Stations

Station	Description
M2b	Noon Gun Area

NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 3.1.2. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). L_{eq} (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods, L_{eq} (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. Supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.
- 3.1.3. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
- One set of measurements between 0700 and 1900 hours on normal weekdays.

MONITORING EQUIPMENT

- 3.1.4. As referred to in the Technical Memorandum (TM) issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.
- 3.1.5. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.2. Air Monitoring

AIR QUALITY MONITORING STATIONS

- 3.2.1. The air monitoring stations for the Project are listed and shown in **Table 3.2** and **Figure 3.1**. **Appendix 3.1** shows the established Action/Limit Levels for the monitoring works.

Table 3.2 Air Monitoring Stations

Station ID	Monitoring Location	Description
CMA3a	CWB PRE Site Office	Causeway Bay

AIR MONITORING PARAMETERS, FREQUENCY AND DURATION

- 3.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 3.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.

. SAMPLING PROCEDURE AND MONITORING EQUIPMENT

- 3.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs
- 3.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:
- 0.6 – 1.7 m3 per minute adjustable flow range;
 - Equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
 - Installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
 - Capable of providing a minimum exposed area of 406 cm²;
 - Flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
 - Equipped with a shelter to protect the filter and sampler;
 - Incorporated with an electronic mass flow rate controller or other equivalent devices;
 - Equipped with a flow recorder for continuous monitoring;
 - Provided with a peaked roof inlet;
 - Incorporated with a manometer;
 - Able to hold and seal the filter paper to the sampler housing at horizontal position;

- Easily changeable filter; and
- Capable of operating continuously for a 24-hour period.

3.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

LABORATORY MEASUREMENT / ANALYSIS

3.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.

3.2.8. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.

3.2.9. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.

3.2.10. All the collected samples shall be kept in a good condition for 6 months before disposal.

3.3. Water Quality Monitoring

3.3.1. The EIA Report has identified that the key water quality impact would be associated with the dredging works during the construction phase. Marine water quality monitoring for dissolved oxygen (DO), suspended solid (SS) and turbidity is therefore recommended to be carried out at selected WSD flushing water intakes. The impact monitoring should be carried out during the proposed dredging works to ensure the compliance with the water quality standards.

Water Quality Monitoring Stations

3.3.2. It is proposed to monitor the water quality at one cooling water intakes along the seafront of the Victoria Harbour. The proposed water quality monitoring stations of the Project are shown in **Table 3.3** and **Figure 3.1**. **Appendix 3.1** shows the established Action/Limit Levels for the monitoring works.

Table 3.3 Marine Water Quality Stations for Water Quality Monitoring

Station Ref.	Location	Easting	Northing
Cooling Water Intake			
C7	Windsor House	837193.7	816150.0

WATER QUALITY PARAMETERS AND FREQUENCY

- 3.3.3. Monitoring of dissolved oxygen (DO), turbidity and suspended solids (SS) shall be carried out at WSD flushing water intakes and cooling water intakes. DO and Turbidity are measured in-situ while SS is determined in laboratory.
- 3.3.4. In association with the water quality parameters, other relevant data shall also be measured, such as monitoring location/position, time, sampling depth, water temperature, pH, salinity, dissolved oxygen (DO) saturation, weather conditions, sea conditions, tidal stage, and any special phenomena and work underway at the construction site etc.

SAMPLING PROCEDURES AND MONITORING EQUIPMENT

- 3.3.5. The interval between two sets of monitoring should not be less than 36 hours except where there are exceedances of Action and/or Limit Levels, in which case the monitoring frequency will be increased. **Table 3.4** shows the proposed monitoring frequency and water quality parameters. Duplicate in-situ measurements and water sampling should be carried out in each sampling event. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.

Table 3.4 Marine Water Quality Monitoring Frequency and Parameters

Activities	Monitoring Frequency ¹	Parameters ²
During the 4-week baseline monitoring period	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
During marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
After completion of marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity

Notes:

- For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.
- Turbidity should be measured in situ whereas SS should be determined by laboratory.

DISSOLVED OXYGEN AND TEMPERATURE MEASURING EQUIPMENT

- 3.3.6. The instrument should be a portable, weatherproof dissolved oxygen measuring instrument complete with cable, sensor, comprehensive operation manuals, and use a DC power source. It should be capable of measuring:

- a dissolved oxygen level in the range of 0-20 mg/l and 0-200% saturation
- a temperature of 0-45 degree Celsius

3.3.7. It should have a membrane electrode with automatic temperature compensation complete with a cable. Sufficient stocks of spare electrodes and cables should be available for replacement where necessary. (e.g. YSI model 59 meter, YSI 5739 probe, YSI 5795A submersible stirrer with reel and cable or an approved similar instrument).

3.3.8. Should salinity compensation not be build-in in the DO equipment, in-situ salinity shall be measured to calibrate the DO equipment prior to each DO measurement.

TURBIDITY MEASUREMENT INSTRUMENT

3.3.9. The instrument should be a portable, weatherproof turbidity-measuring instrument complete with comprehensive operation manual. The equipment should use a DC power source. It should have a photoelectric sensor capable of measuring turbidity between 0-1000 NTU and be complete with a cable (e.g. Hach model 2100P or an approved similar instrument).

SAMPLER

3.3.10. A water sampler comprises a transparent PVC cylinder, with a capacity of not less than 2 litres, and can be effectively sealed with latex cups at both ends. The sampler should have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth (e.g. Kahlsico Water Sampler or an approved similar instrument).

SAMPLE CONTAINER AND STORAGE

3.3.11. Water samples for suspended solids measurement should be collected in high-density polythene bottles, packed in ice (cooled to 4°C without being frozen), and delivered to ALS Technichem (HK) Pty Ltd. as soon as possible after collection for analysis.

WATER DEPTH DETECTOR

3.3.12. A portable, battery-operated echo sounder shall be used for the determination of water depth at each designated monitoring station. This unit can either be handheld or affixed to the bottom of the workboat, if the same vessel is to be used throughout the monitoring programme.

SALINITY

3.3.13. A portable salinometer capable of measuring salinity in the range of 0-40 ppt shall be provided for measuring salinity of the water at each of monitoring location.

MONITORING POSITION EQUIPMENT

3.3.14. A hand-held or boat-fixed type digital Global Positioning System (GPS) with waypoint bearing indication or other equivalent instrument of similar accuracy shall be provided and used during monitoring to ensure the monitoring vessel is at the correct location before taking measurements.

CALIBRATION OF IN-SITU INSTRUMENTS

- 3.3.15. All in-situ monitoring instrument shall be checked, calibrated and certified by a laboratory accredited under HOKLAS or equivalent before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the water quality monitoring. Responses of sensors and electrodes should be checked with certified standard solutions before each use. Wet bulb calibration for a DO meter shall be carried out before measurement at each monitoring location.
- 3.3.16. For the on site calibration of field equipment by the ET, the BS 127:1993, "Guide to Field and on-site test methods for the analysis of waters" should be observed.
- 3.3.17. Sufficient stocks of spare parts should be maintained for replacements when necessary. Backup monitoring equipment shall also be made available so that monitoring can proceed uninterrupted even when some equipment is under maintenance, calibration, etc.

LABORATORY MEASUREMENT / ANALYSIS

- 3.3.18. Analysis of suspended solids has been carried out in a HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd. Water samples of about 1L shall be collected at the monitoring stations for carrying out the laboratory SS determination. The SS determination work shall start within 24 hours after collection of the water samples. The SS determination shall follow APHA 19ed or equivalent methods subject to the approval of IEC and EPD.

4. MONITORING RESULTS

4.0.1. Overall layout showing work areas and monitoring stations are shown in [Figure 2.1](#) and [Figure 3.1](#).

4.1. Noise Monitoring Results

4.1.1. The commencement date of dredging work was 25 November 2011. Noise monitoring was commenced on 29 November 2011.

4.1.2. The noise monitoring station is shown in [Table 4.1](#) below:

Table 4.1 Noise Monitoring Stations

Station	Description
M2b	Noon Gun Area

4.1.3. There was no exceedance recorded in reporting quarter. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of graphical presentation can be referred in [Appendix 4.1](#).

4.2. Air Monitoring Results

4.2.1. The commencement date of dredging work was 25 November 2011. Air quality monitoring was commenced on 25 November 2011.

4.2.2. The air monitoring stations is shown in [Table 4.2](#) below.

Table 4.2 Air Monitoring Stations

Station	Description
CMA3a	CWB PRE Site Office

4.2.3. No action and limit level exceedances were recorded in the reporting quarter. Details of air monitoring results and graphical presentation can be referred in [Appendix 4.2](#).

4.3. Water Monitoring Results

4.3.1. The commencement date of dredging work was 25 November 2011. Water quality monitoring was commenced on 25 November 2011. The water quality monitoring station is summarized in [Table 4.3](#) below:

Table 4.3 Water Monitoring Station

Station Ref.	Location	Easting	Northing
Cooling Water Intake			
C7	Windsor House	837193.7	816150.0

- 4.3.3 Two limit level turbidity exceedances and two limit level suspended solid exceedances at C7 were recorded in this reporting quarter. All exceedances were considered related to project works. Details of water quality monitoring results and graphical presentation can be referred in **Appendix 4.3**.

December 2013 Reporting Month

- 4.3.4 One limit level turbidity and one suspended solid exceedances were recorded on 4 December 2013 during flood tide. After investigation, the exceedances were considered as works-related due to installation of rebar for EVA at Eastern Breakwater and dredging of type II marine sediment.
- 4.3.5 One limit level turbidity and one suspended solid exceedances were recorded on 16 December 2013 during flood tide. After investigation, the exceedances were considered works-related due to dredging action of unwinding silt curtain installed around the silt screen.

January 2014 Reporting Month

- 4.3.6 No exceedance was recorded in the reporting month.

February 2014 Reporting Month

- 4.3.7 No exceedance was recorded in the reporting month.

4.4 Waste Monitoring Results

- 4.4.1 Inert C&D waste was disposed & no Non-inert C&D wastes were disposed of in this reporting period. Details of the waste flow table are summarized in **Table 4.4**

Table 4.4 Details of Waste Disposal

Waste Type*	Quantity this Quarter, m ³	Cumulative-to-Date, m ³	Location of Disposal
Inert C&D materials disposed, m ³	NIL NIL	32,670 6,267	TM38 TKO137
Inert C&D materials recycled, m ³	NIL NIL NIL NIL	25,395.7 1,228 1416 352 1,049	TS2 WDII Lun Ku Tan WENT Landfill HY/2011/03 (H2M)
Non-inert C&D materials disposed, m ³	NIL	NIL	N/A
Non-inert C&D materials recycled, m ³	NIL	NIL	N/A
Chemical waste disposed, kg	NIL	NIL	N/A
Marine Sediment	NIL	10,640	Cheung Chau South

Waste Type*	Quantity this Quarter, m ³	Cumulative-to-Date, m ³	Location of Disposal
(Type 1 – Open Sea Disposal), m ³	(Bulk Volume)	(Bulk Volume)	
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal), m ³	NIL (Bulk Volume)	7,500 (Bulk Volume)	East of Sha Chau
Marine Sediment (Type 3 – Special Treatment / Disposal contained in geosynthetic Containers), m ³	NIL	NIL	N/A

4.4.2 There were no marine sediments Type 1 – Open Sea Disposal and Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal in the reporting quarter.

5. COMPLIANCE AUDIT

- 5.0.1. The Event Action Plan for construction noise, air quality and water quality are presented in **Appendix 5.1.**

4.5 Noise Monitoring

- 4.5.3 [No exceedance](#) was recorded in the reporting quarter.

4.6 Air Monitoring

- 5.2.1. [No exceedance](#) were recorded in the reporting quarter.

4.7 Water Quality Monitoring

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

[December 2013 Reporting Month](#)

- 4.7.1 [Two limit level turbidity and two suspended solid exceedances were recorded at C7 in December reporting month. The exceedances were considered as works-related.](#)

[January 2014 Reporting Month](#)

- 4.7.2 [No exceedance was recorded in the reporting month.](#)

[February 2014 Reporting Month](#)

- 4.7.3 [No exceedance was recorded in the reporting month.](#)

4.8 Site Audit

- 5.4.1. There was no non-compliance from the site audits in the reporting quarter.

6. COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION

- 6.0.1. There was no environmental complaint received in this quarter.
- 6.0.2. The details of cumulative complaint log and summary of complaints are presented in **Appendix 6.1**.
- 6.0.3. No notification of summons or prosecution was received in the reporting period. Cumulative statistic on complaints and successful prosecutions are summarized in **Table 6.1** and **Table 6.2** respectively.

Table 6.1 Cumulative Statistics on Complaints

Reporting Period	No. of Complaints
25 Nov 2011 (Commencement of work) – 27 February 2014	0
Project-to-Date	0

Table 6.2 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this quarter (Offence Date)	Cumulative No. Project-to-Date
Air	-	0	0
Noise	-	0	0
Water	-	0	0
Waste	-	0	0
Total	-	0	0

7. CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS

- 7.0.1. According to Condition 3.4 of the EP-416/2011, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Wan Chai Development Phase II (WDII) and Central-WanChai Bypass (CWB).
- 7.0.2. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activity under Wan Chai Development Phase II were marine works at HKCEC areas, cross-harbour Watermains, Fresh Watermains and Cooling Watermains Installations, tunnel works at Wan Chai East. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were [tunnel construction at TS4 and tunnel construction and dismantling of struts at TPCWAE](#), [Bridge construction and tunnel works at Central Interchange](#), [ELS segment launching works and tunnel works at North Point area](#). The major environmental impact was water quality impact at Causeway Bay and Wan Chai. Land-based construction activities were [tunnel works at TS2](#), [ELS work and tunnel construction at TS4 and tunnel construction and dismantling of struts at TPCWAE](#), tunnel works at Central and ELS work at North Point and tunnel works at Wan Chai East in the reporting month.


8. CONCLUSION

- 8.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alternations to the programme proposed were made in response to changing circumstances.
- 8.0.2. No non-compliances were noted and no prosecutions were received during the reporting quarter.
- 8.0.3. No project-related exceedances were recorded during the reporting quarter.
- 8.0.4. No environmental complaint and prosecution recorded in the reporting quarter.
- 8.0.5. The construction programme is provided in [Appendix 7.1](#).



Figure 2.1

Project Layout

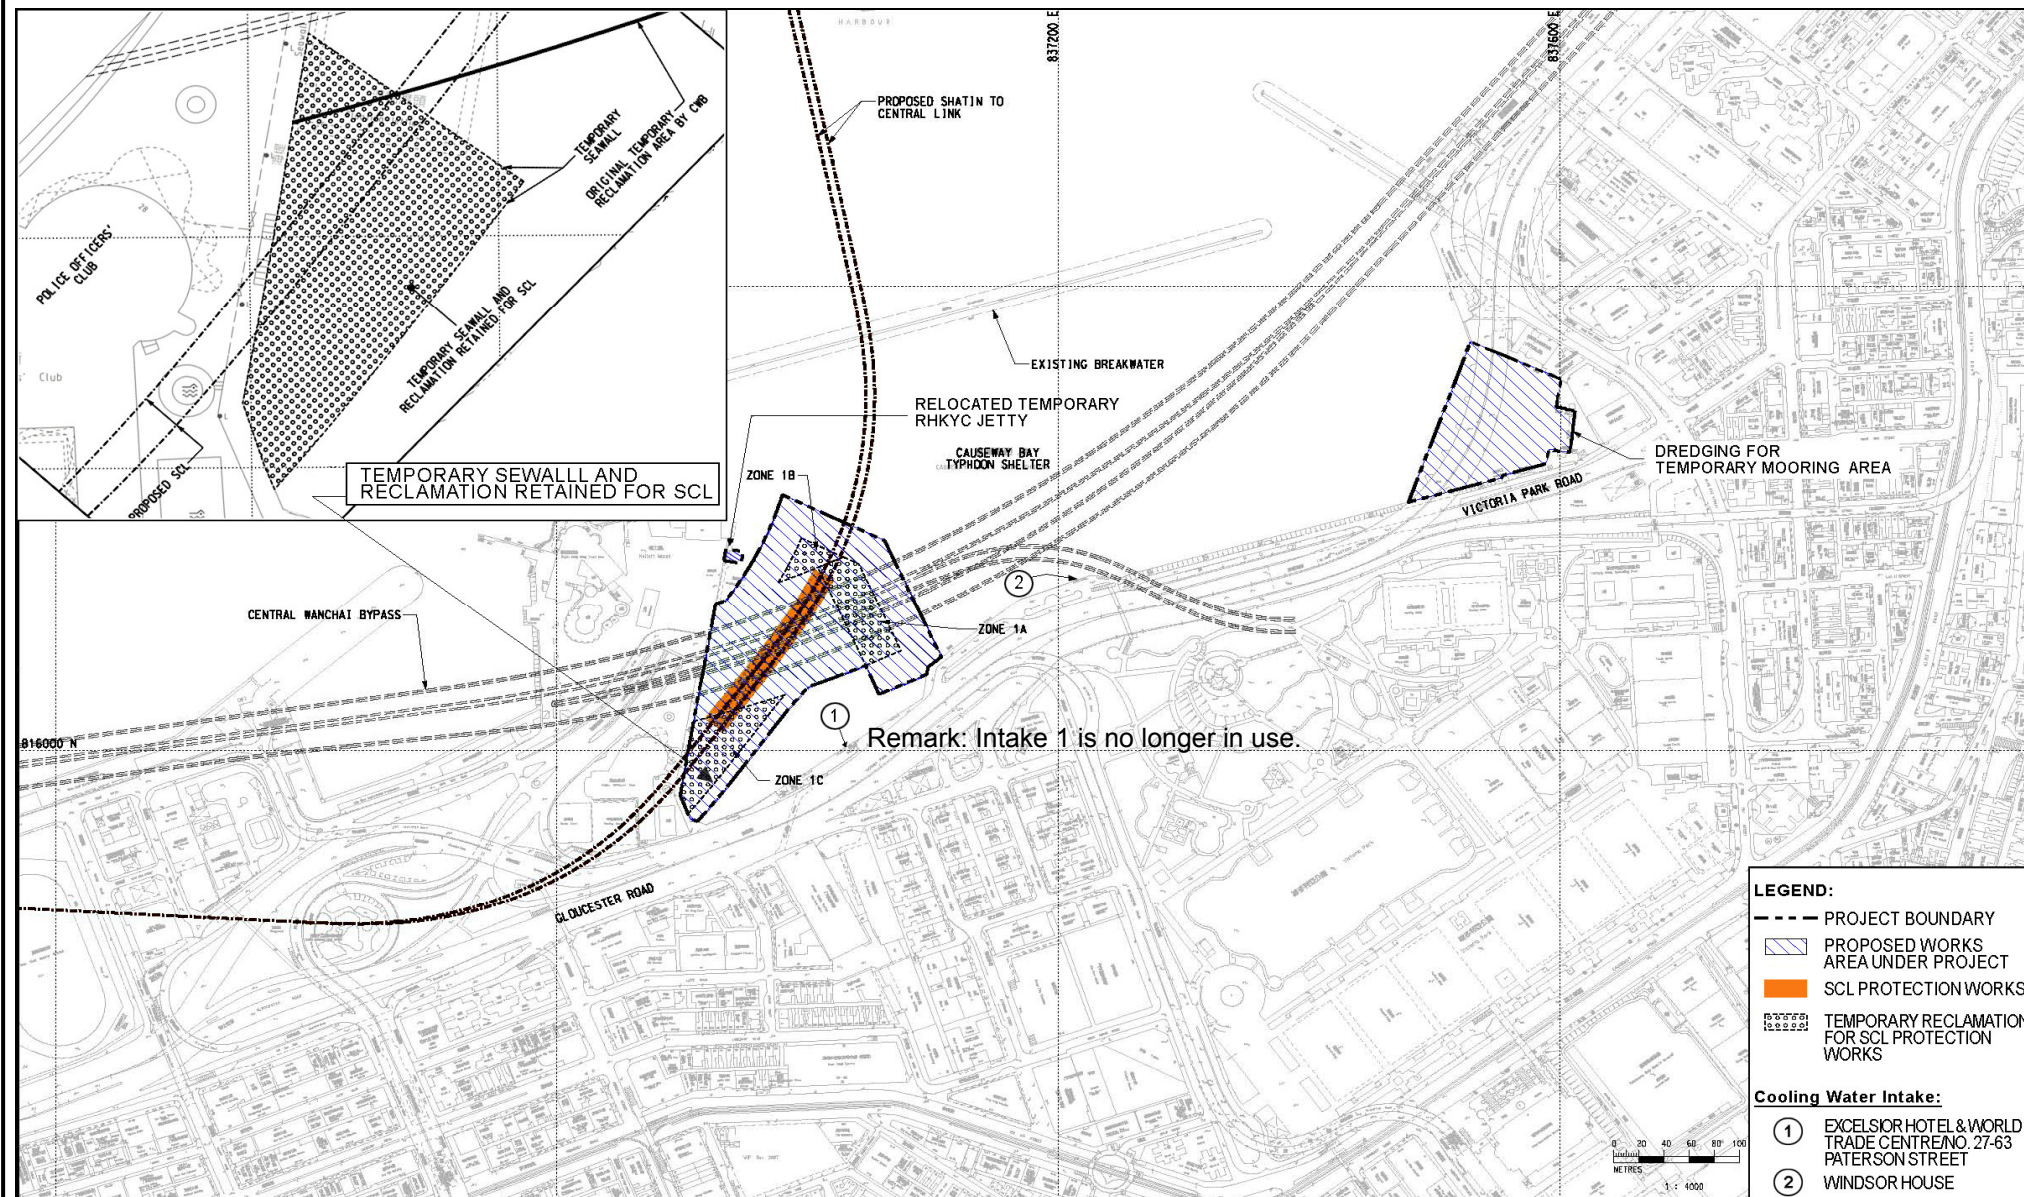

Project Title : ShaTin to Central Link Protection Works at Causeway Bay Typhoon Shelter
 工程項目名稱：沙田至中環綫位於銅鑼灣避風塘內之保護工程

Environmental Permit No. : EP-416/2011
 環境許可證編號 : EP-416/2011

Figure 1: Location of the Project
圖 1: 工程項目位置

(This figure was prepared based on Figure NEX2213/C/331/ENS/M50/501 of EIA report (Register No.: AEIAR-159/2011))
 (本圖是根據環評報告(登記冊編號 AEIAR-159/2011) 圖 NEX2213/C/331/ENS/M50/501 編制)



Figure 2.2

Project Organization Chart



Project Organization Chart


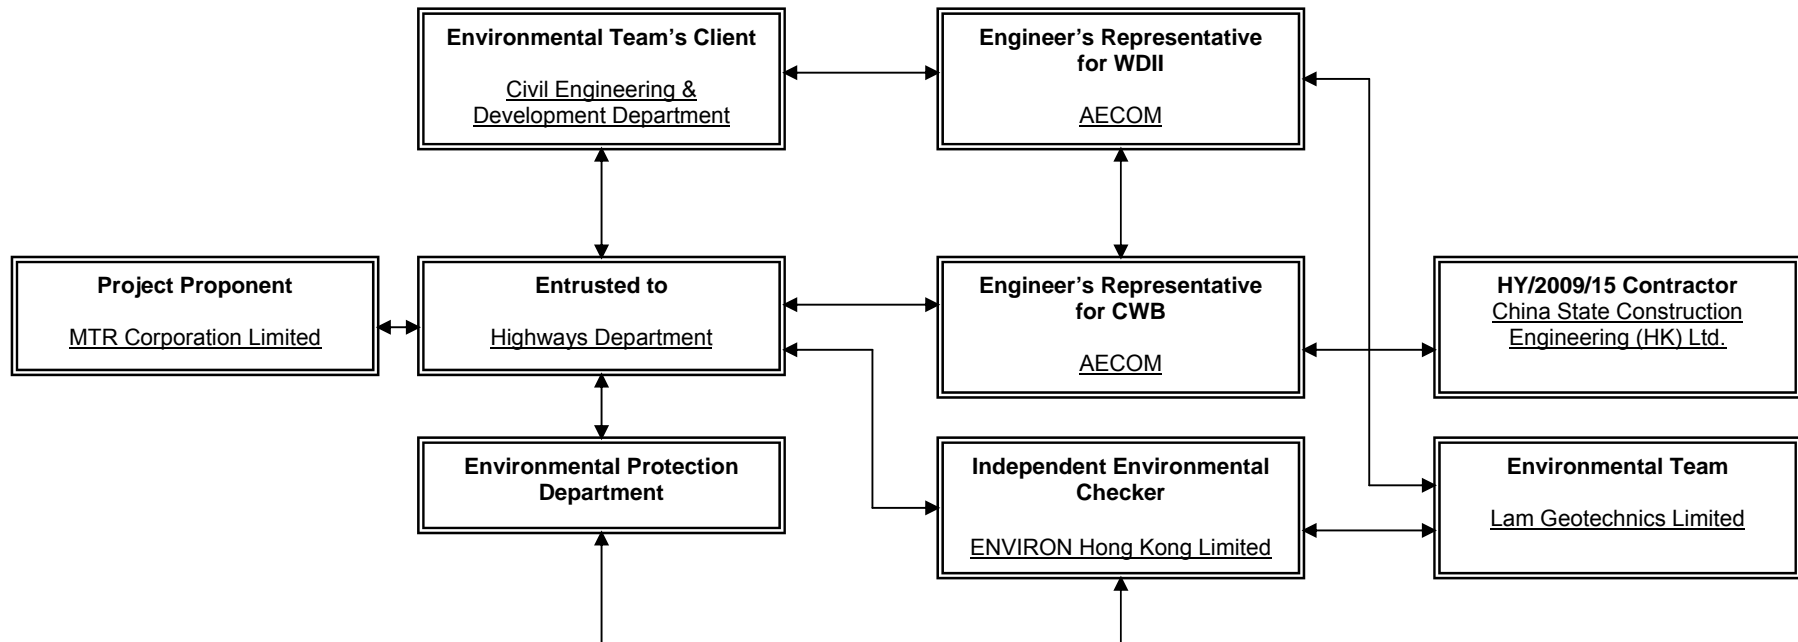




Figure 3.1

Locations of Monitoring Stations



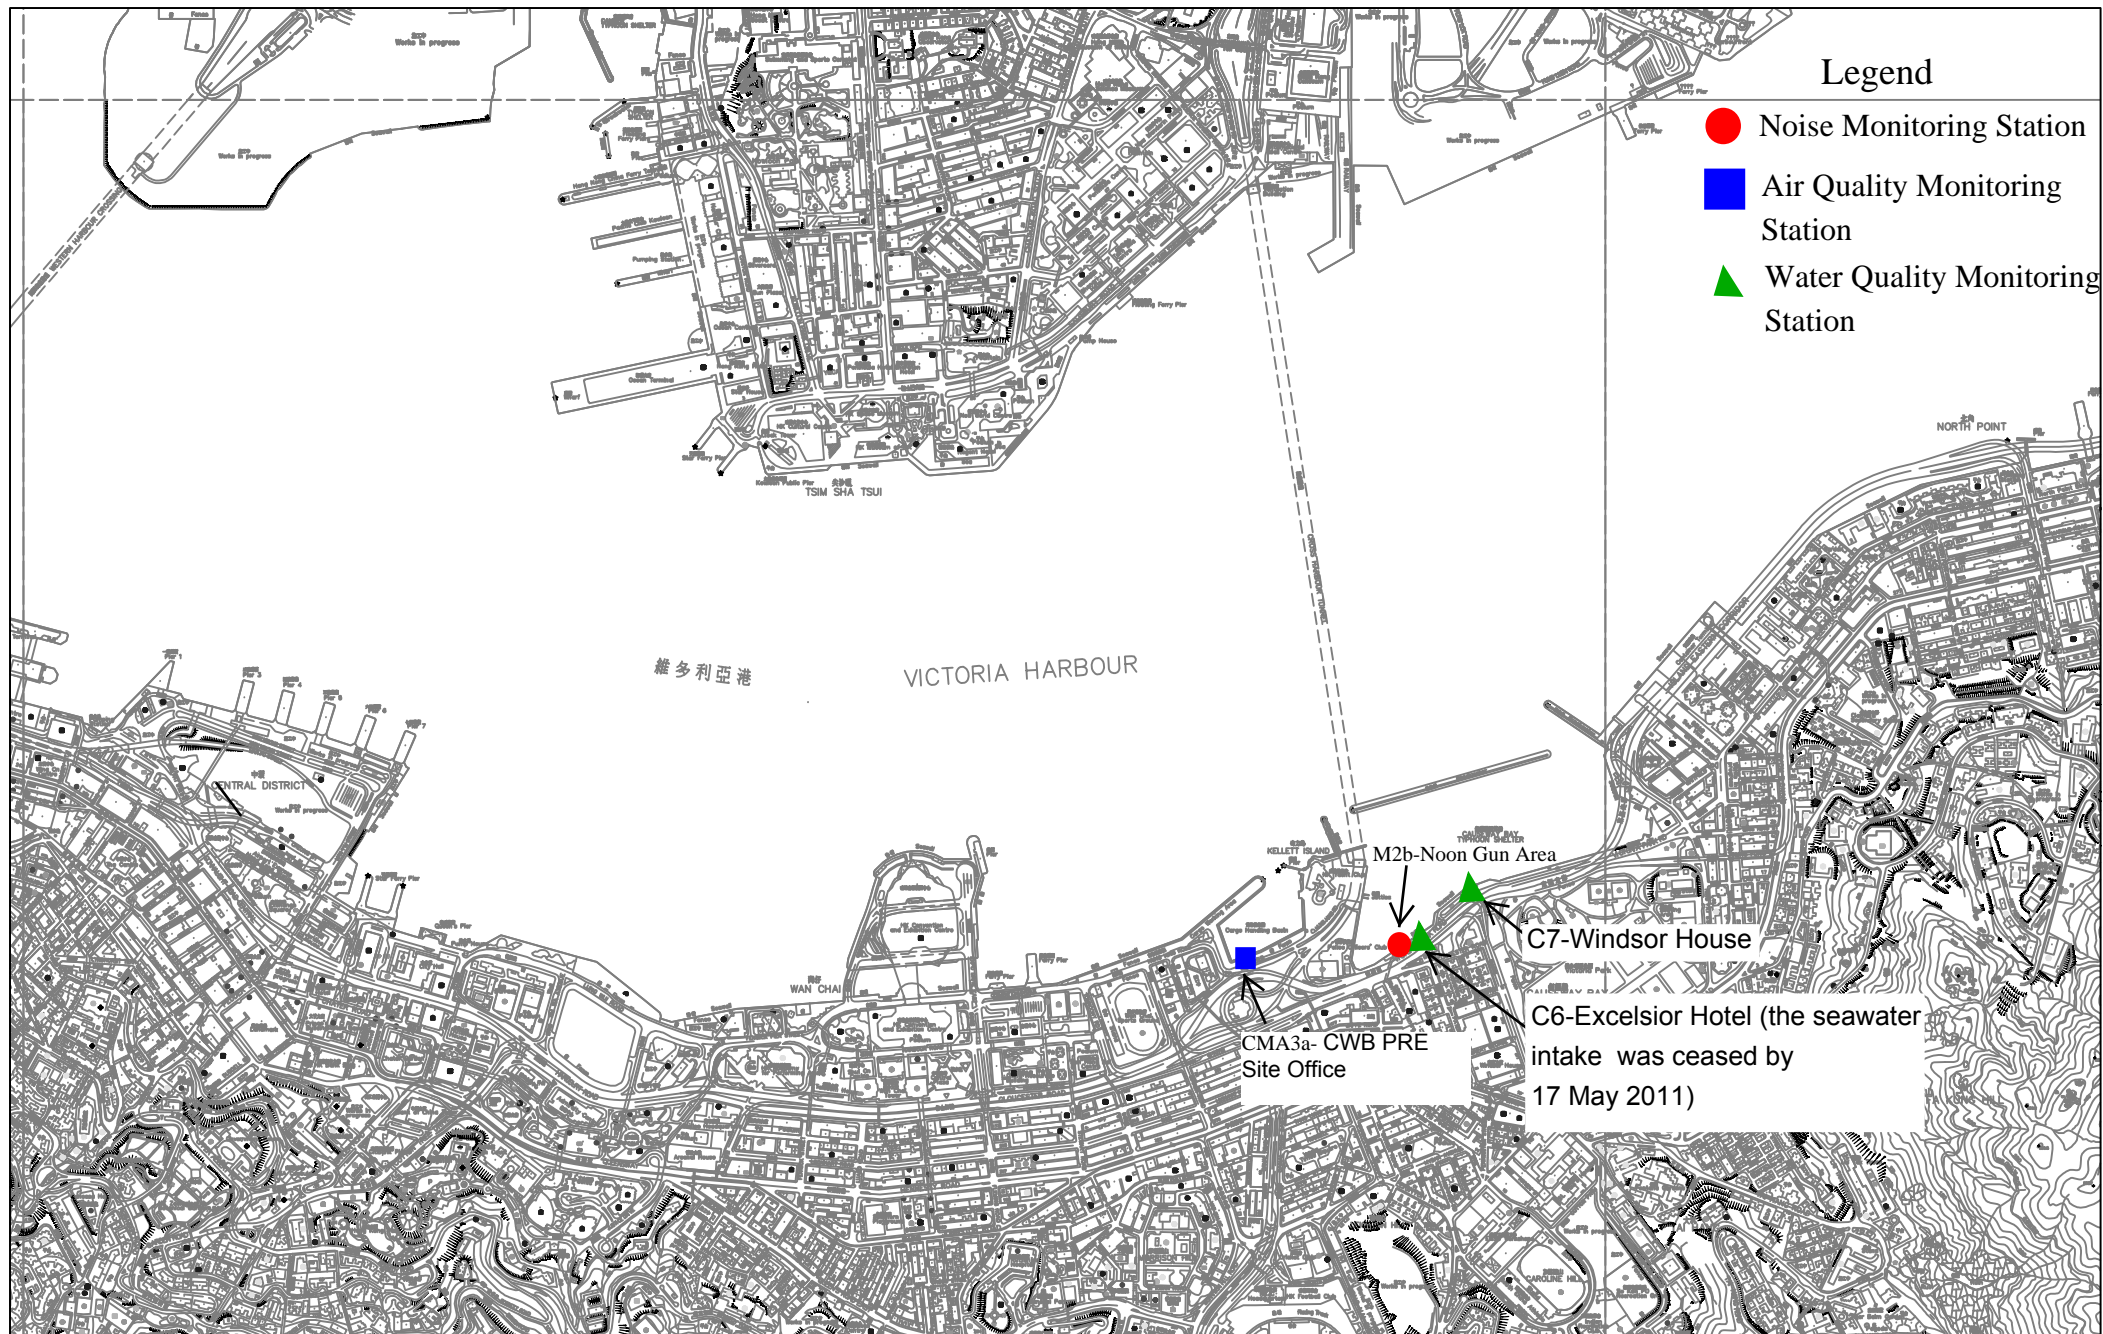

Appendix 2.1

Environmental Mitigation Implementation Schedule

IMPLEMENTATION SCHEDULE OF THE PROPOSED MITIGATION MEASURES

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve?
Water Quality Impact (Construction Phase)						
3.142	Dredging should be carried out by closed grab dredger.	To minimize release of sediment and contaminants during dredging.	Contractor	Dredging works areas in Causeway Bay Typhoon Shelter (CBTS)	Construction Phase	EIAO-TM, WPCO
S3.142	All temporary reclamation works should adopt an approach where temporary seawalls will first be formed to enclose each phase of the temporary reclamation. Installation of diaphragm wall on temporary reclamation as well as any bulk filling will proceed behind the completed seawall. Any gaps that may need to be provided for marine access should be shielded by silt curtains to control sediment plume dispersion away from the site. Demolition of temporary reclamation including the demolition of the diaphragm wall and dredging to the existing seabed levels	To minimize loss of fines and contaminants during temporary reclamations	Contractor	Temporary reclamation works areas in CBTS	Construction Phase	EIAO-TM, WPCO

	should be carried out behind the temporary seawall. Temporary seawall should be removed after completion of all excavation and dredging works for demolition of the temporary reclamation.					
S3.142	During construction of the temporary reclamation, temporary seawall should be partially constructed to protect the nearby seawater intakes from further dredging activities. For example, the seawalls along the southeast and northeast boundaries of PW1.1 should be constructed first (above high water mark) so that the seawater intake at the inner water would be protected from the impacts from the remaining dredging activities along the northwest boundary.	To minimize water quality impact upon the cooling water intakes in CBTS from temporary reclamation works	Contractor	Temporary reclamation works areas in CBTS	Construction Phase	EIAO-TM, WPCO
S3.142	Silt curtains should be deployed to fully enclose the closed grab dredger during any dredging operation within the CBTS.	To minimize loss of fines and contaminants during dredging in CBTS	Contractor	Dredging works areas in CBTS	Construction Phase	EIAO-TM, WPCO
S3.142	Silt screens will be installed at all the cooling water intakes within the CBTS during temporary reclamation and dredging within the typhoon shelter.	To minimize water quality impact upon the cooling water intakes in CBTS from marine construction activities	Contractor	Cooling water intakes inside CBTS	Construction Phase	EIAO-TM, WPCO
S3.143	No more than two closed grab dredgers should be operated for dredging within the CBTS at	To minimize loss of fines and contaminants	Contractor	Temporary reclamation and	Construction Phase	EIAO-TM, WPCO

	any time. Moreover, the combined production rate of all concurrent dredging works to be undertaken within the CBTS shall not exceed 6,000 m ³ per day at all times throughout the entire construction period.	dredging in CBTS		dredging works areas in CBTS		
S3.145	<p>The following good site practices should be undertaken during sand filling, public filling and dredging:</p> <ul style="list-style-type: none"> • mechanical grabs, if used, should be designed and maintained to avoid spillage and sealed tightly while being lifted. For dredging of any contaminated mud, closed watertight grabs must be used; • all vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; • all hopper barges and dredgers should be fitted with tight fitting seals to their bottom openings to prevent leakage of material; • construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the 	To minimize loss of fines and contaminants from dredging / filling	Contractor	Temporary reclamation and dredging works areas in CBTS	Construction Phase	EIAO-TM, WPCO

	site or dumping grounds; and <ul style="list-style-type: none"> loading of barges and hoppers should be controlled to prevent splashing of dredged material into the surrounding water. Barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation. 					
S3.146	The following mitigation measures are proposed to minimize the potential water quality impacts from the construction works at or close to the seafront: <ul style="list-style-type: none"> Temporary storage of construction materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction and demolition materials should be located well away from the seawater front and storm drainage during carrying out of the works. Stockpiling of construction and demolition materials and dusty materials should be covered and located away from the seawater front and storm drainage. Construction debris and spoil should be covered up and/or disposed of as soon as 	To minimize release of construction wastes from construction works at or close to the seafront	Contractor	Construction works at or close to the seafront	Construction Phase	EIAO-TM, WPCO

	possible to avoid being washed into the nearby receiving waters.					
S3.147	Silt curtains should be installed around the working area for the marine piling works for construction of the temporary jetty as necessary to minimize the release of sediment and construction wastes. All wastewater generated from the piling activities should be collected by a derrick lighter or other collection system and be treated before controlled discharge. Spoil from the piling activities should be collected by sealed hopper barges for proper disposal.	To minimize water quality impacts from piling works for construction of the temporary jetty	Contractor	Piling area at the piling location	Construction Phase	EIAO-TM, WPCO
S3.148	Regular maintenance of and refuse collection should be performed at the silt screens deployed at the seawater intakes at regular intervals on a daily basis. The Contractor should be responsible for keeping the water behind the silt screen free from floating rubbish and debris during the impact monitoring period.	To avoid the pollutant and refuse entrapment problems at the silt screens to be installed at the water intakes	Contractor	Proposed silt screens at cooling water intakes inside CBTS	Construction Phase	EIAO-TM, WPCO
S3.149	It is recommended that collection and removal of floating refuse should be performed within the marine construction areas at regular intervals on a daily basis. The Contractor should be	To minimize water quality impacts from illegal dumping and littering from marine vessels and runoff from	Contractor	All marine works areas	Construction Phase	EIAO-TM, WPCO, WDO

	responsible for keeping the water within the site boundary and the neighbouring water free from rubbish during the dredging works.	the coastal areas				
S3.150 to 3.169	The site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" should be followed where practicable.	To minimize water quality impacts from construction site runoff and general construction activities	Contractor	All construction works areas	Construction Phase	EIAO-TM, WPCO, TM-DSS, WDO, ProPECC PN 1/94
S3.170	There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. Minimum distances of 100 m should be maintained between the discharge points of construction site effluent and the existing seawater intakes. The beneficial uses of the treated effluent for other on-site activities such as dust suppression, wheel washing and general cleaning etc., can minimise water consumption	To minimize water quality impact from effluent discharges from construction sites	Contractor	All construction works areas	Construction Phase	EIAO-TM, WPCO, TM-DSS

	and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of Regional Office (RO) of EPD.					
S3.171 & 3.172	Construction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. If disposal of sewage to public sewerage system is not feasible, appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the construction workers over the construction site to prevent direct disposal of sewage into the water environment. The Contractor shall also be responsible for waste disposal and maintenance practices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment.	To minimize water quality impacts due to sewage generated from construction workforce	Contractor	All construction works areas	Construction Phase	EIAO-TM, WPCO, TM-DSS, WDO
S3.173	Contractor must register as a chemical waste producer if	To minimize water quality	Contractor	All construction	Construction Phase	EIAO-TM, WPCO, TM-

	chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	impact from accidental spillage of chemical		works areas		DSS, WDO
S3.174	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	To minimize water quality impact from accidental spillage of chemical	Contractor	All construction works areas	Construction Phase	EIAO-TM, WPCO, TM-DSS, WDO
S3.175	Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The "Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes" published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows: <ul style="list-style-type: none"> Suitable containers should 	To minimize water quality impact from accidental spillage of chemical	Contractor	All construction works areas	Construction Phase	EIAO-TM, WPCO, TM-DSS, WDO

	<p>be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</p> <ul style="list-style-type: none"> • Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents. • Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area. 					
S4. 30	<p>The following good site practices should be implemented:</p> <ul style="list-style-type: none"> • Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program • Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program • Mobile plant, if any, should be sited as far from NSRs as possible • Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum 	To reduce construction noise impact	Contractor	All works areas	Construction phase	EIAO-TM, NCO

	<ul style="list-style-type: none"> Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities. 					
S4.31 – S4.32 & Table 4.7	<p>The following quiet PME are recommended for the construction activities:</p> <p>Air Compressor Bulldozer Concrete Pump Concrete Lorry Mixer Crane Dump Truck Excavator Generator Hand-held Breaker Poker Vibrator Roller Trucks</p>	To reduce construction noise impact	Contractor	All works areas	Construction phase	EIAO-TM, NCO
S4.33 – S4.35 & Table 4.8	<p>Movable noise barrier should be used for the following PME:</p> <p>Air Compressor Bar Bender Bentonite Plants Concrete pump Diaphragm Wall Rigs Excavator</p>	To reduce construction noise impact	Contractor	Affected works areas showing exceedance during un-mitigated scenario	Construction phase	EIAO-TM, NCO

	Poker Vibrator					
Construction Dust Impact						
S5.43	Watering once on construction areas for every working hour	To minimize dust impact	Contractor	Temporary reclamation area in CBTS	Construction phase	APCO
S5.43	Covering/paving the southwest retained area of temporary reclamation once filling is completed	To minimize dust impact	Contractor	southwest retained area of temporary reclamation	Construction phase	phase APCO
S5.44	<p>Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices:</p> <p>Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather.</p> <p>Use of frequent watering for particularly dusty construction areas and areas close to ASRs.</p> <p>Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.</p>	To minimize dust impacts	Contractor	Temporary reclamation area in CBTS	Construction phase	APCO and Air Pollution Control (Construction Dust) Regulation

	<p>Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs.</p> <p>Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.</p> <p>Establishment and use of vehicle wheel and body washing facilities at the exit points of the site.</p> <p>Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods.</p> <p>Provision of not less than 2.4m high hoarding from ground level along site boundary where adjoins a road, streets or other accessible to the public except for a site entrance or exit.</p> <p>Imposition of speed controls for vehicles on site haul roads.</p> <p>Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs.</p>					
--	---	--	--	--	--	--

	<p>Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.</p> <ul style="list-style-type: none"> • Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise. 					
Waste Management implications (Construction Phase)						
6.62	<p>Good Site Practices and Waste Reduction Measures</p> <ul style="list-style-type: none"> - Prepare a Waste Management Plan approved by the Engineer/Supervising Officer of the Project based on current practices on construction sites; - Training of site personnel in, site cleanliness, proper waste management and chemical handling procedures; - Provision of sufficient waste disposal points and regular collection of waste; - Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; - Regular cleaning and 	To enhance water management practice and achieve waste reduction.	Contractor	All Work Sites	Construction Phase	Waste Disposal Ordinance (Cap. 354) Land (Miscellaneous Provisions) Ordinance (Cap. 28) ETWB TC(W) No.31/2004

	<p>maintenance programme for drainage systems, sumps and oil interceptors; and</p> <ul style="list-style-type: none"> - Separation of chemical wastes for special handling and appropriate treatment. 					
6.63	<p>Good Site Practices and Waste Reduction Measures (con't)</p> <ul style="list-style-type: none"> - Sorting of demolition debris and excavated materials from demolition works to recover reusable/ recyclable portions (i.e. soil, broken concrete, metal etc.); - Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; - Encourage collection of aluminum cans by providing separate labeled bins to enable this waste to be segregated from other general refuse generated by the workforce; - Proper storage and site practices to minimize the potential for damage or contamination of construction materials; - Plan and stock construction 	To achieve waste reduction	Contractor	All Work Sites	Construction Phase	<p>Waste Disposal Ordinance (Cap. 354)</p> <p>Land (Miscellaneous Provisions) Ordinance (Cap. 28)</p>

	materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste; and - Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycle.					
6.64	<i>Good Site Practices and Waste Reduction Measures (con't)</i> - The Contractor shall prepare and implement an EMP in accordance with ETWB TCW No. 19/2005. Such management plan should incorporate site specific factors, such as the designation of areas for segregation and temporary storage of reusable and recyclable materials. The EMP should be submitted to the Engineer for approval. The Contractor should implement the waste management practices in the EMP throughout the construction stage of the Project. The EMP should be reviewed regularly and updated by the Contractor, preferably in a monthly basis.	To enhance water management practice and achieve waste reduction.	Contractor	All Work Sites	Construction Phase	ETWB TCW No. 19/2005

6.66	<i>Storage, Collection and Transportation of Waste</i> - Waste, such as soil, should be handled and stored well to ensure secure containment, thus minimizing the potential of pollution; - Maintain and clean storage areas routinely; - Stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; and - Different locations should be designated to stockpile each material to enhance reuse.	To minimize potential adverse environmental impacts arising from waste storage	Contractor	Work Sites	Construction Phase	-
6.67	<i>Storage, Collection and Transportation of Waste (con't)</i> - Waste haulier with appropriate permits should be employed by the Contractor for the collection and transportation of waste from works areas to respective disposal outlets.	To minimize potential adverse environmental impacts arising from waste collection and disposal	Contractor	Waste storage area.	Construction Phase	-
6.68	<i>Storage, Collection and Transportation of Waste (con't)</i> - Implementation of trip ticket system with reference to ETWB TC(W) No.31/2004 to monitor disposal of waste and to control fly-tipping at PFRFs or landfills.	To minimize potential adverse environmental impacts arising from waste collection and disposal	Contractor	Work Sites	Construction Phase	ETWB TC(W) No.31/2004

	A recording system for the amount of waste generated, recycled and disposed (including disposal sites) should be proposed.					
6.70 – 6.73	Sorting of C&D Materials <ul style="list-style-type: none"> - Sorting to be performed to recover the inert materials, reusable and recyclable materials before disposal off-site. - Specific areas should be provided by the Contractors for sorting and to provide temporary storage areas for the sorted materials. - The C&D materials should at least be segregated into inert and non-inert materials, in which the inert portion could be reused and recycled as far as practicable before delivery to PFRFs as mentioned for beneficial use in other projects. While opportunities for reusing the non-inert portion should be investigated before disposal of at designated landfills. - Possibility of reusing the spoil in the Project will be continuously investigated in the construction stage. 	To minimize potential adverse environmental impacts during the handling, transportation and disposal of C&D materials	Contractor	All work Sites	Construction Phase	ETWB TCW No. 31/2004 ETWB TCW No. 33/2002 ETWB TCW No. 19/2005
6.75	Sediments <ul style="list-style-type: none"> - The basic requirements and procedures for dredged 	To ensure the sediment to be disposed of in an	Contractor	All works areas with sediments	Construction Phase	PNAP 252

	sediment disposal specified under PNAP 252 shall be followed. MFC manages disposal facilities in Hong Kong for the dredged sediment, while EPD is the authority issuing marine dumping permits under the <i>Dumping at Sea Ordinance</i> .	authorized and least impacted way		concern		
6.76	<p>Sediments (con't)</p> <p>- The Project Proponent should agree in advance with MFC of CEDD on the site allocation by submitting a Construction & Demolition Material Management Plan. The contractor for the dredging works shall then apply for the site allocations of marine sediment disposal based on the prior agreement with MFC/CEDD. A request for reservation of sediment disposal space has been submitted to MFC for onward discussions of disposal approaches and feasible disposal sites. The Project Proponent is also responsible for application of all necessary permits from the relevant authorities, including the dumping permit as required under DASO from EPD, for the disposal of dredged sediment prior to the commencement of the dredging works.</p>	To determine the best handling and disposal option of the sediments	MTR / Contractor	All works areas with sediments concern	Prior to the start of dredging works	PNAP 252; Dumping at Sea Ordinance

6.77 – 6.81	<p><i>Sediments (con't)</i></p> <ul style="list-style-type: none"> - Requirements of the Air Pollution Ordinance (Construction Dust) Regulation, where relevant, shall be adhered to during dredging, transportation and disposal of sediments. - Stockpiling of contaminated sediments should be avoided as far as possible. If temporary stockpiling of contaminated sediments is necessary, the dredged sediment should be covered by tarpaulin and the area should be placed within earth bunds or sand bags to prevent leachate from entering the ground, nearby drains and/or surrounding water bodies. The stockpiling areas should be completely paved or covered by linings in order to avoid contamination to underlying soil or groundwater. Separate and clearly defined areas should be provided for stockpiling of contaminated and uncontaminated materials. Leachate, if any, should be collected and discharged according to the Water Pollution Control Ordinance (WPCO). - In order to minimise the potential odour / dust emissions during dredging and 	To ensure handling of sediments are in accordance to statutory requirements	Contractor	Work Sites, Sediment disposal sites	Construction Phase	PNAP 252 Dumping at Sea Ordinance
----------------	---	---	------------	-------------------------------------	--------------------	-----------------------------------

	<p>transportation of the sediment, the dredged sediments should be properly covered when placed on barges. Loading of the dredged sediment to the barge should be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding water.</p> <ul style="list-style-type: none"> - The barge transporting the sediments to the designated disposal sites should be equipped with tight fitting seals to prevent leakage and should not be filled to a level that would cause overflow of materials or laden water during loading or transportation. In addition, monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the DEP. - In order to minimise the exposure to contaminated materials, workers should wear appropriate personal protective equipments (PPE) when handling contaminated sediments. Adequate washing and cleaning facilities should also be provided on site. 					
--	---	--	--	--	--	--

6.82	<i>Sediments (con't)</i> The dredging work and associate sediment handling under this Project will be undertaken together with the CWB project by Highways Department and geosynthetic containment will be adopted to handle Type 3 sediments.	To ensure handling of sediments are in accordance to statutory requirements	Contractor	Work Sites, Sediment disposal sites	Construction Phase	PNAP 252 Dumping at Sea Ordinance
6.86	<i>Containers for Storage of Chemical Waste</i> The Contractor should register with EPD as a chemical waste producer and to follow the guidelines stated in the <i>Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes</i> . Containers used for storage of chemical waste should: <ul style="list-style-type: none"> - Be compatible with the chemical wastes being stored, maintained in good condition and securely sealed; - Have a capacity of less than 450 litters unless the specifications have been approved by EPD; and 	To register with EPD as a Chemical waste producer and store chemical waste in appropriate containers	Contractor	Chemical waste storage area	Construction Phase	Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes

	- Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Waste Disposal (Chemical Waste) (General) Regulation.					
6.87	Chemical Waste Storage Area - Be clearly labeled to indicate corresponding chemical characteristics of the chemical waste and used for storage of chemical waste only; - Be enclosed on at least 3 sides; - Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; - Have adequate ventilation; - Be covered to prevent rainfall from entering; and - Be properly arranged so that incompatible materials are adequately separated.	To prepare appropriate storage areas for chemical waste at works areas	Contractor	Chemical waste storage area	Construction Phase	Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
6.88	Labelling of Chemical Waste - Lubricants, waste oils and other chemical wastes would be generated during the maintenance of vehicles and mechanical equipments. Used	To clearly label the chemical waste at works areas	Contractor	Chemical waste storage area	Construction Phase	Code of Practice on the Packaging, Labelling and Storage of Chemical

	lubricants should be collected and stored in individual containers which are fully labeled in English and Chinese and stored in a designated secure place.					Wastes
6.89	<i>Collection and Disposal of Chemical Waste</i> - A trip-ticket system should be operated in accordance with the <i>Waste Disposal (Chemical Waste) (General) Regulation</i> to monitor all movements of chemical waste. The Contractor shall employ a licensed collector to transport and dispose of the chemical wastes, to either the approved CWTC at Tsing Yi, or another licensed facility, in accordance with the <i>Waste Disposal (Chemical Waste) (General) Regulation</i> .	To monitor the generation, reuse and disposal of chemical waste	Contractor	Work Sites with chemical waste production	Construction Phase	Waste Disposal (Chemical Waste) (General) Regulation
6.90	<i>General Refuse</i> - General refuse should be stored in enclosed bins or compaction units separate from C&D materials and chemical waste. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D materials and chemical wastes. Preferably, an enclosed and	To properly store and separate from other C&D materials for subsequent collection and disposal	Contractor	All Work Sites	Construction Phase	-

	covered area should be provided to reduce the occurrence of windblown light material.					
6.91	General Refuse (con't) - The recyclable component of general refuse, such as aluminum cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.	To facilitate recycling of recyclable portions of refuse	Contractor	All Work Sites	Construction Phase	-
6.92	General Refuse (con't) - The Contractor should carry out an education programme for workers in avoiding, reducing, reusing and recycling of materials generation. Posters and leaflets advising on the use of the bins should also be provided in the sites as reminders.	To raise workers' awareness on recycling issue	Contractor	All Work Sites	Construction Phase	-



Appendix 3.1

Action and Limit Level



Action and Limit Level

Action and Limit Level for Air Quality Monitoring

1-hour TSP Level in $\mu\text{g}/\text{m}^3$		24-hour TSP Level in $\mu\text{g}/\text{m}^3$	
Action Level	Limit Level	Action Level	Limit Level
311.3	500	171.0	260

Action and Limit Level for Noise Monitoring

Time Period	Action Level	Limit Level
07:00 – 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A)/ 70 dB(A)/ 65 dB(A) ^{Note 1}

Note 1:

- 70dB(A) and 65 dB(A) for schools during normal teaching periods and school examination periods, respectively.
- If works are to be carried out during the restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

Action and Limit Level for Water Quality Monitoring

Parameters	Dry Season		Wet Season	
	Action Level	Limit Level	Action Level	Limit Level
Cooling Water Intake				
SS in mg/L	15.00	22.13	18.42	27.54
Turbidity in NTU	9.10	10.25	11.35	12.71
DO in mg/L	3.36	2.73	3.02	2.44

Remarks: - Contractor shall implement additional improvement measures in case of oxygen depletion (i.e. DO level <2 mg/L) detected within CBTS.



Appendix 4.1

Noise Monitoring Graphical Presentations



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M2b - Noon-day gun area

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level		Limit Level
			Leq	L10	L90	Leq		Leq	Leq
			Unit: dB(A), (30-min)						
4/12/2013	9:32	Fine	70.0	72.0	67.0	68		66	75
10/12/2013	16:40	Fine	69.7	71.5	66.5	68		66	75
18/12/2013	8:40	Fine	67.9	71.3	61.4	68		56	75
23/12/2013	10:07	Fine	74.2	76.5	69.0	68		73	75



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M2b - Noon-day gun area

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
31/12/2013	9:00	Fine	69.7	71.0	67.5	68	66	75
7/1/2014	13:25	Fine	71.7	73.5	68.5	68	70	75
14/1/2014	9:55	Fine	70.3	71.0	69.0	68	67	75
22/1/2014	15:35	Fine	73.3	75.0	70.0	68	72	75
28/1/2014	11:11	Fine	74.0	77.5	68.0	68	73	75



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M2b - Noon-day gun area

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level		Limit Level
			Leq	L10	L90	Leq	Leq	Leq	
			Unit: dB(A), (30-min)						
4/2/2014	13:54	Fine	67.1	68.5	65.0	68	67	75	
10/2/2014	16:15	Cloudy	70.4	72.5	67.5	68	67	75	
18/2/2014	14:06	Fine	69.9	71.0	67.5	68	66	75	
25/2/2014	13:15	Fine	69.6	72.0	67.5	68	65	75	




Contract No. HK/2011/07

Wanchai Development Phase II and Central Wanchai Bypass
(Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter)

Graphic Presentation of Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

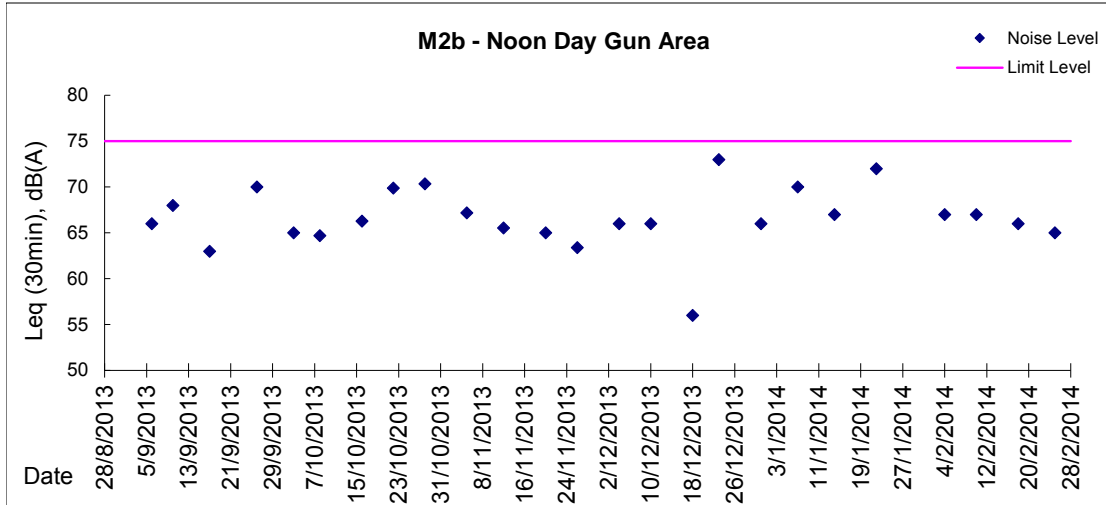



Appendix 4.2
Air Quality Monitoring Graphical Presentations



Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 171
Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
2-Dec-13	8:00	Fine	005985	2.6523	2.8642	898.89	922.89	24.00	1.38	1.38	1.38	1985	107
7-Dec-13	8:00	Fine	005966	2.6469	2.9128	925.89	949.89	24.00	1.38	1.37	1.38	1981	134
13-Dec-13	8:00	Cloudy	005969	2.6538	2.9725	952.87	976.87	24.00	1.38	1.38	1.38	1983	161
19-Dec-13	8:00	Cloudy	007807	2.6310	2.7575	979.87	1003.87	24.00	1.41	1.41	1.41	2033	62
23-Dec-13	8:00	Cloudy	006679	2.6478	2.9284	1006.87	1030.87	24.00	1.41	1.41	1.41	2027	138

Report on 1-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 311.3
Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Dec-13	8:45	Fine	006248	2.6073	2.6217	922.89	923.89	1.00	1.38	1.38	1.38	83	174
3-Dec-13	9:48	Fine	006250	2.6275	2.6405	923.89	924.89	1.00	1.38	1.38	1.38	83	157
3-Dec-13	10:55	Fine	006475	2.7223	2.7329	924.89	925.89	1.00	1.34	1.34	1.34	81	132
9-Dec-13	10:00	Fine	006235	2.6686	2.6846	949.89	950.89	1.00	1.37	1.37	1.37	82	194
9-Dec-13	13:00	Fine	007671	2.6512	2.6669	950.89	951.89	1.00	1.37	1.37	1.37	82	191
9-Dec-13	15:00	Fine	005806	2.7709	2.7924	951.89	952.89	1.00	1.34	1.34	1.34	80	268
14-Dec-13	8:40	Rainy	007813	2.6499	2.6648	976.87	977.87	1.00	1.38	1.38	1.38	83	180
14-Dec-13	9:45	Rainy	007811	2.6289	2.6439	977.87	978.87	1.00	1.38	1.38	1.38	83	181
14-Dec-13	10:55	Rainy	007809	2.6484	2.6632	978.87	979.87	1.00	1.34	1.34	1.34	81	184
20-Dec-13	8:40	Cloudy	007672	2.6435	2.6534	1003.87	1004.87	1.00	1.41	1.41	1.41	85	117
20-Dec-13	9:45	Cloudy	006683	2.6595	2.6700	1004.87	1005.87	1.00	1.41	1.41	1.41	85	124
20-Dec-13	10:57	Cloudy	006445	2.7282	2.7408	1005.87	1006.87	1.00	1.38	1.38	1.38	83	152
24-Dec-13	8:48	Rainy	007805	2.6333	2.6481	1030.87	1031.87	1.00	1.41	1.41	1.41	84	175
24-Dec-13	10:34	Rainy	007803	2.6550	2.6689	1031.87	1032.87	1.00	1.41	1.41	1.41	84	165
24-Dec-13	14:17	Rainy	006469	2.7456	2.7581	1032.87	1033.87	1.00	1.37	1.37	1.37	82	152

Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 171
Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
28-Dec-13	8:00	Fine	006471	2.7317	3.0684	1033.87	1057.87	24.00	1.42	1.42	1.42	2047	164
3-Jan-14	8:00	Fine	007525	2.6233	2.9673	1060.87	1084.87	24.00	1.41	1.41	1.41	2032	169
9-Jan-14	8:00	Cloudy	007512	2.6455	2.9139	1087.87	1111.87	24.00	1.42	1.42	1.42	2042	131
15-Jan-14	8:00	Fine	007572	2.6320	2.8376	1114.87	1138.87	24.00	1.42	1.42	1.42	2045	101
20-Jan-14	8:00	Fine	007768	2.6637	3.0081	1141.87	1165.87	24.00	1.42	1.42	1.42	2042	169
24-Jan-14	8:00	Fine	007773	2.6478	2.8303	1168.87	1192.87	24.00	1.42	1.41	1.41	2037	90

Report on 1-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 311.3
Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
30-Dec-13	9:17	Fine	007530	2.6326	2.6423	1057.87	1058.87	1.00	1.39	1.39	1.39	83	117
30-Dec-13	10:23	Fine	007529	2.6328	2.6447	1058.87	1059.87	1.00	1.42	1.42	1.42	85	140
30-Dec-13	13:00	Fine	007527	2.6136	2.6319	1059.87	1060.87	1.00	1.39	1.39	1.39	83	220
4-Jan-14	8:20	Fine	006443	2.7984	2.8136	1084.87	1085.87	1.00	1.38	1.38	1.38	83	184
4-Jan-14	9:25	Fine	006447	2.7478	2.7645	1085.87	1086.87	1.00	1.41	1.41	1.41	85	197
4-Jan-14	10:30	Fine	007756	2.6570	2.6720	1086.87	1087.87	1.00	1.38	1.38	1.38	83	181
10-Jan-14	8:45	Cloudy	006392	2.6917	2.7164	1111.87	1112.87	1.00	1.42	1.42	1.42	85	290
10-Jan-14	9:49	Cloudy	006389	2.7026	2.7210	1112.87	1113.87	1.00	1.42	1.42	1.42	85	216
10-Jan-14	10:55	Cloudy	006387	2.6205	2.6351	1113.87	1114.87	1.00	1.42	1.42	1.42	85	172
16-Jan-14	9:20	Fine	007776	2.6274	2.6389	1138.87	1139.87	1.00	1.42	1.42	1.42	85	135
16-Jan-14	10:25	Fine	006388	2.6044	2.6174	1139.87	1140.87	1.00	1.42	1.42	1.42	85	153
16-Jan-14	13:00	Fine	007770	2.6388	2.6493	1140.87	1141.87	1.00	1.42	1.42	1.42	85	123
21-Jan-14	8:25	Fine	007772	2.6416	2.6573	1165.87	1166.87	1.00	1.42	1.42	1.42	85	184
21-Jan-14	9:30	Fine	007777	2.6457	2.6601	1166.87	1167.87	1.00	1.42	1.42	1.42	85	169
21-Jan-14	10:40	Fine	007778	2.6229	2.6372	1167.87	1168.87	1.00	1.42	1.42	1.42	85	168
25-Jan-14	8:25	Cloudy	004929	2.7857	2.7999	1192.87	1193.87	1.00	1.41	1.41	1.41	85	167
25-Jan-14	10:55	Cloudy	005934	2.6477	2.6634	1193.87	1194.87	1.00	1.41	1.41	1.41	85	185
25-Jan-14	13:00	Cloudy	007690	2.6509	2.6615	1194.87	1195.87	1.00	1.41	1.41	1.41	85	125



Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 171
Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
29-Jan-14	8:00	Fine	006442	2.7538	2.9158	1195.87	1219.87	24.00	1.41	1.41	1.41	2035	80
4-Feb-14	8:00	Cloudy	007828	2.8307	2.9718	1222.87	1246.87	24.00	1.41	1.41	1.41	2034	69
10-Feb-14	8:00	Cloudy	007857	2.8492	3.0322	1249.88	1273.88	24.00	1.42	1.42	1.42	2051	89
15-Feb-14	8:00	Cloudy	007765	2.6409	2.7870	1276.88	1300.88	24.00	1.42	1.42	1.42	2044	71
21-Feb-14	8:00	Cloudy	007836	2.8414	3.0450	1303.87	1327.87	24.00	1.41	1.41	1.41	2031	100
27-Feb-14	8:00	Cloudy	007967	2.8577	2.9515	1330.87	1354.87	24.00	1.40	1.40	1.40	2019	46

Report on 1-hour TSP monitoring
Action Level ($\mu\text{g}/\text{m}^3$) - 311.3
Limit Level ($\mu\text{g}/\text{m}^3$) - 500


Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
30-Jan-14	9:25	Fine	007720	2.6698	2.6808	1219.87	1220.87	1.00	1.41	1.41	1.41	85	130
30-Jan-14	10:42	Fine	007917	2.8573	2.8671	1220.87	1221.87	1.00	1.41	1.41	1.41	85	116
30-Jan-14	13:00	Fine	007697	2.6359	2.6514	1221.87	1222.87	1.00	1.41	1.41	1.41	85	183
5-Feb-14	8:31	Cloudy	007856	2.8540	2.8555	1246.87	1247.87	1.00	1.41	1.41	1.41	85	18
5-Feb-14	9:36	Cloudy	007863	2.8364	2.8408	1247.87	1248.87	1.00	1.41	1.41	1.41	85	52
5-Feb-14	10:40	Cloudy	007861	2.8452	2.8469	1248.87	1249.87	1.00	1.41	1.41	1.41	85	20
11-Feb-14	8:20	Cloudy	006315	2.6373	2.6473	1273.88	1274.88	1.00	1.42	1.42	1.42	85	117
11-Feb-14	9:23	Cloudy	006316	2.6079	2.6231	1274.88	1275.88	1.00	1.42	1.42	1.42	85	178
11-Feb-14	10:27	Cloudy	006317	2.6197	2.6349	1275.88	1276.88	1.00	1.42	1.42	1.42	85	178
17-Feb-14	8:11	Cloudy	007833	2.8368	2.8421	1300.88	1301.88	1.00	1.41	1.41	1.41	85	63
17-Feb-14	9:17	Cloudy	007834	2.8661	2.8746	1301.88	1302.88	1.00	1.41	1.41	1.41	85	100
17-Feb-14	10:20	Cloudy	007835	2.8400	2.8484	1302.88	1303.88	1.00	1.41	1.41	1.41	85	99
22-Feb-14	8:21	Cloudy	007971	2.8460	2.8574	1327.87	1328.87	1.00	1.38	1.38	1.38	83	138
22-Feb-14	9:57	Cloudy	007907	2.8469	2.8580	1328.87	1329.87	1.00	1.38	1.38	1.38	83	134
22-Feb-14	10:59	Cloudy	007908	2.8235	2.8358	1329.87	1330.87	1.00	1.38	1.38	1.38	83	149
28-Feb-14	9:35	Cloudy	005481	2.8055	2.8157	1354.87	1355.87	1.00	1.40	1.40	1.40	84	121
28-Feb-14	10:50	Cloudy	005483	2.7985	2.8091	1355.87	1356.87	1.00	1.40	1.40	1.40	84	126
28-Feb-14	13:00	Cloudy	005485	2.7871	2.7967	1356.87	1357.87	1.00	1.40	1.40	1.40	84	114




Contract No. HK/2011/07

Wanchai Development Phase II and Central Wanchai Bypass
(Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter)

Graphic Presentation of 1 hour TSP Result

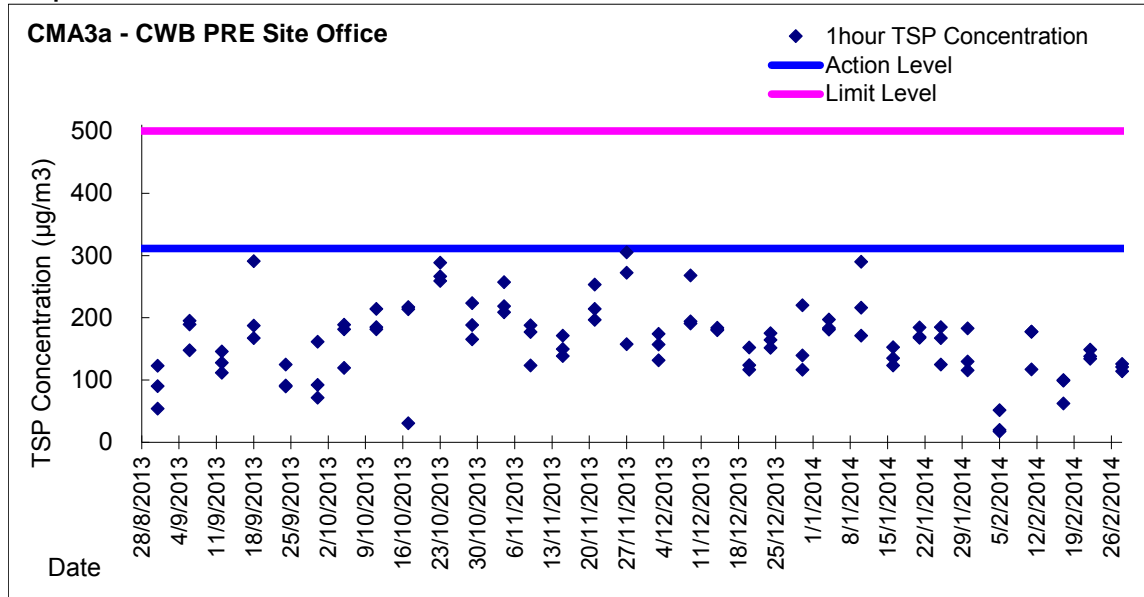

Graphic Presentation of 24 hour TSP Result

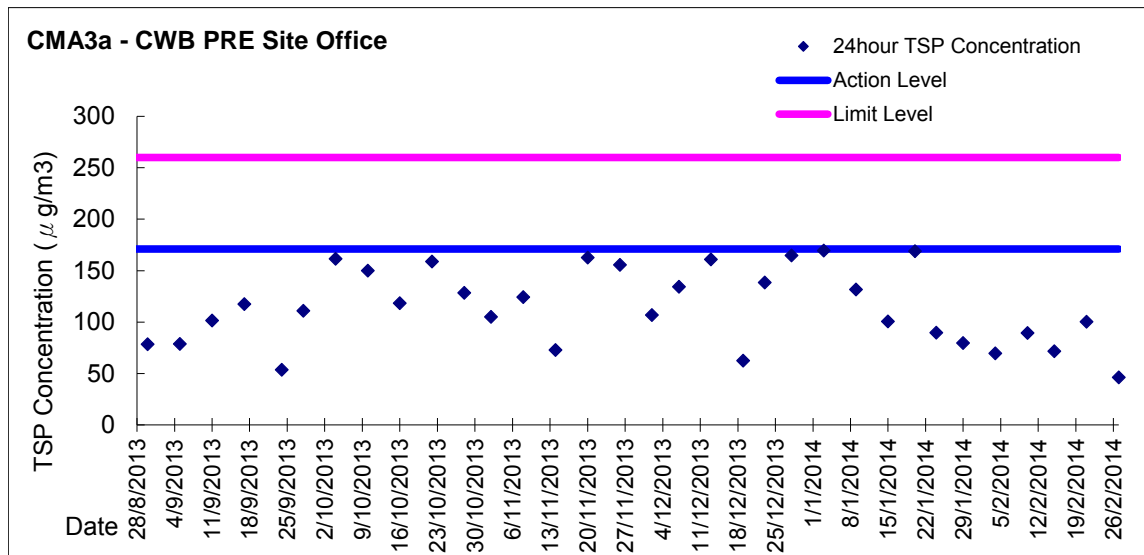



Appendix 4.3

Water Quality Monitoring Graphical Presentations



**Water Monitoring Result at C7 - Windsor House
Mid-Flood Tide**

Date	Time	Weater Condition	Sampling Depth		Water Temperature		pH		Salinity		DO Saturation		DO		Turbidity		Suspended Solids							
					°C		-		ppt		%		mg/L		NTU		mg/L							
			m		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average						
2013-11-28	14:15	Fine	Middle	1.5	21.40	21.40	21.40	7.97	7.97	7.97	31.09	31.09	31.09	57.5	58.2	58.1	4.25	4.30	4.30	1.25	1.26	1.24	6	5.50
	14:17		Middle	1.5	21.40	21.40		7.97	7.97		31.09	31.09		58.2	58.6		4.30	4.33		1.25	1.21		5	
2013-11-30	15:02	Fine	Middle	1.5	21.00	21.00	21.00	8.06	8.06	8.05	31.32	31.32	31.32	60.1	60.5	60.5	4.47	4.50	4.50	3.78	3.76	3.75	3	3.00
	15:04		Middle	1.5	21.00	21.00		8.04	8.04		31.32	31.32		60.7	60.7		4.51	4.50		3.74	3.73		3	
2013-12-02	15:30	Fine	Middle	1.5	21.60	21.60	21.60	8.06	8.06	8.06	31.74	31.74	31.74	70.1	70.4	70.5	5.16	5.17	5.17	5.53	5.45	5.46	3	4.00
	15:32		Middle	1.5	21.60	21.60		8.06	8.06		31.74	31.74		70.7	70.8		5.17	5.18		5.42	5.42		5	
2013-12-04	19:25	Fine	Middle	1.5	20.00	20.00	19.95	8.13	8.13	8.13	32.75	32.75	32.75	69.4	70.6	70.0	5.21	5.31	5.26	14.78	14.81	14.76	23	23.00
	19:26		Middle	1.5	19.90	19.90		8.13	8.13		32.76	32.75		69.9	70.1		5.25	5.27		14.75	14.70		23	
2013-12-07	11:32	Fine	Middle	1.5	20.90	20.90	20.90	8.05	8.05	8.05	31.68	31.68	31.68	62.5	62.6	62.4	4.64	4.64	4.63	2.85	2.81	2.81	4	4.00
	11:34		Middle	1.5	20.90	20.90		8.05	8.05		31.68	31.68		62.3	62.3		4.62	4.62		2.78	2.80		4	
2013-12-09	12:47	Fine	Middle	1.5	22.00	22.00	22.15	8.02	8.02	8.01	31.89	31.89	31.89	63.1	63.5	64.6	4.58	4.61	4.68	4.85	4.88	4.90	11	11.00
	12:49		Middle	1.5	22.30	22.30		8.00	8.00		31.89	31.89		65.0	66.7		4.70	4.83		4.91	4.95		11	
2013-12-11	16:17	Fine	Middle	1.5	21.50	21.50	21.60	8.03	8.03	8.02	31.81	31.81	31.81	61.5	62.1	61.6	4.50	4.54	4.51	3.06	3.04	3.04	4	3.50
	16:19		Middle	1.5	21.70	21.70		8.01	8.01		31.80	31.80		61.6	61.3		4.50	4.48		3.03	3.02		3	
2013-12-13	15:47	Cloudy	Middle	1.5	20.80	20.80	20.80	8.14	8.14	8.14	32.63	32.63	32.62	59.7	59.8	60.0	4.41	4.43	4.44	3.21	3.18	3.17	2	2.00
	15:49		Middle	1.5	20.80	20.80		8.14	8.14		32.60	32.60		60.3	60.1		4.46	4.45		3.14	3.13		2	
2013-12-16	15:52	Cloudy	Middle	1.5	18.10	18.10	18.10	8.23	8.23	8.23	32.05	32.05	32.05	62.1	62.6	62.8	4.85	4.89	4.91	39.13	39.13	39.13	66	65.50
	15:54		Middle	1.5	18.10	18.10		8.23	8.23		32.05	32.05		63.4	63.2		4.96	4.94		39.13	39.14		65	
2013-12-18	16:22	Fine	Middle	1.5	18.20	18.20	18.20	8.35	8.35	8.35	34.19	34.19	34.19	64.7	65.4	65.3	4.98	5.03	5.03	2.50	2.51	2.51	2	2.00
	16:24		Middle	1.5	18.20	18.20		8.35	8.35		34.19	34.19		65.4	65.6		5.04	5.05		2.50	2.52		<2	
2013-12-21	10:32	Fine	Middle	1.5	18.40	18.40	18.40	8.47	8.47	8.47	35.14	35.14	35.14	71.4	72.0	71.8	5.44	5.48	5.47	5.19	5.20	5.22	4	4.50
	10:34		Middle	1.5	18.40	18.40		8.47	8.47		35.14	35.14		72.1	71.6		5.49	5.46		5.22	5.25		5	
2013-12-24	12:02	Fine	Middle	1.5	18.50	18.50	18.50	8.42	8.42	8.42	35.26	35.26	35.27	56.1	56.8	56.7	4.29	4.31	4.31	4.08	4.09	4.08	5	4.00
	12:04		Middle	1.5	18.50	18.50		8.41	8.41		35.27	35.27		56.8	57.1		4.31	4.34		4.08	4.06		3	
2013-12-26	10:20	Fine	Middle	1.0	17.60	17.60	17.55	8.32	8.32	8.32	31.97	31.96	32.01	62.8	63.4	63.2	4.95	5.00	4.99	6.93	6.98	6.96	6	6.50
	10:21		Middle	1.0	17.50	17.50		8.31	8.31		32.05	32.05		63.6	63.0		5.02	4.98		6.97	6.95		7	

Remarks:

Single underline denotes exceedance over Action Level.

Double underline denotes exceedance over Limit Level.



Water Monitoring Result at C7 - Windsor House
Mid-Ebb Tide

Date	Time	Weater Condition	Sampling Depth		Water Temperature			pH			Salinity			DO Saturation			DO			Turbidity			Suspended Solids	
			m		°C		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average		
					Value	Average																	Value	Average
28/11/2013	10:30	Cloudy	Middle	2	20.30	20.30	20.25	7.94	7.94	7.94	30.40	30.40	30.40	69.9	70.1	69.7	5.29	5.30	5.27	2.93	2.93	2.93	9	8.50
	10:32		Middle	2	20.20	20.20		7.93	7.93		30.40	30.40		69.3	69.3		5.24	5.24		2.93	2.94		8	
30/11/2013	11:22	Fine	Middle	2	20.80	20.80	20.75	8.06	8.06	8.05	31.68	31.68	31.68	62.3	61.1	61.6	4.64	4.59	4.61	1.61	1.57	1.57	6	6.00
	11:24		Middle	2	20.70	20.70		8.04	8.04		31.68	31.68		61.1	62.0		4.59	4.61		1.54	1.55		6	
02/12/2013	1:50	Fine	Middle	1	19.40	19.40	19.40	7.96	7.96	7.96	31.15	31.15	31.16	51.8	51.9	51.5	3.97	3.97	3.94	2.37	2.32	2.35	3	3.00
	1:51		Middle	1	19.40	19.40		7.96	7.96		31.16	31.16		50.9	51.5		3.89	3.94		2.42	2.27		3	
04/12/2013	14:52	Fine	Middle	2	21.60	21.60	21.75	8.09	8.09	8.09	31.62	31.62	31.62	71.2	71.5	71.4	5.20	5.24	5.22	5.24	5.22	5.22	7	6.00
	14:54		Middle	2	21.90	21.90		8.08	8.08		31.61	31.61		71.6	71.2		5.24	5.20		5.21	5.21		5	
07/12/2013	4:03	Fine	Middle	1	19.30	19.30	19.25	8.20	8.20	8.19	31.86	31.86	31.86	69.8	69.8	70.5	5.36	5.34	5.25	1.61	1.58	1.62	3	3.50
	4:04		Middle	1	19.20	19.20		8.18	8.18		31.86	31.86		71.1	71.2		5.14	5.15		1.64	1.65		4	
09/12/2013	4:48	Fine	Middle	1	21.00	21.00	21.00	8.17	8.17	8.17	30.58	30.58	30.58	57.4	57.3	57.4	4.27	4.31	4.29	1.56	1.41	1.37	4	4.50
	4:49		Middle	1	21.00	21.00		8.17	8.16		30.58	30.58		57.7	57.3		4.30	4.26		1.26	1.23		5	
11/12/2013	20:05	Cloudy	Middle	2	20.10	20.10	20.10	8.12	8.13	8.12	32.16	32.21	32.20	61.5	61.9	61.9	4.51	4.56	4.55	3.19	3.25	3.24	<2	<2
	20:06		Middle	2	20.10	20.10		8.12	8.12		32.21	32.21		62.0	62.0		4.56	4.56		3.22	3.28		<2	
13/12/2013	23:20	Cloudy	Middle	1	20.40	20.40	20.40	8.26	8.26	8.24	31.69	31.69	31.69	68.7	69.2	69.0	5.15	5.18	5.16	2.01	2.13	2.00	<2	<2
	23:21		Middle	1	20.40	20.40		8.22	8.22		31.69	31.69		69.3	68.6		5.19	5.13		1.91	1.94		<2	
17/12/2013	1:58	Cloudy	Middle	1	16.90	16.90	16.90	8.20	8.20	8.20	26.48	26.48	26.48	48.2	49.0	48.9	3.97	4.04	4.03	3.45	3.47	3.41	<2	<2
	1:59		Middle	1	16.90	16.90		8.19	8.20		26.48	26.48		49.1	49.1		4.05	4.05		3.40	3.31		<2	
19/12/2013	3:22	Fine	Middle	1	15.00	15.00	14.98	8.15	8.15	8.15	28.30	28.30	28.51	51.7	52.0	52.0	4.36	4.41	4.40	2.88	2.92	2.95	9	7.00
	3:23		Middle	1	14.90	15.00		8.15	8.15		28.74	28.71		52.1	52.2		4.41	4.41		3.00	2.98		5	
21/12/2013	3:11	Fine	Middle	1	16.90	16.90	16.90	8.11	8.11	8.11	29.50	29.50	29.50	50.3	50.4	50.4	4.08	4.08	4.09	2.84	2.87	2.86	3	4.00
	3:12		Middle	1	16.90	16.90		8.10	8.10		29.50	29.50		50.4	50.5		4.09	4.09		2.88	2.83		5	
24/12/2013	3:15	Fine	Middle	1	16.50	16.50	16.50	8.14	8.14	8.14	31.37	31.37	31.38	60.6	61.0	61.3	4.00	4.06	4.50	2.06	2.03	2.02	3	2.50
	3:16		Middle	1	16.50	16.50		8.14	8.14		31.39	31.39		61.9	61.7		4.99	4.96		2.00	1.98		2	
26/12/2013	5:45	Fine	Middle	1	15.90	15.90	15.90	8.13	8.13	8.13	30.92	30.92	30.92	49.0	49.3	49.2	4.02	4.04	4.04	1.41	1.45	1.47	<2	<2
	5:46		Middle	1	15.90	15.90		8.12	8.12		30.92	30.92		49.3	49.3		4.04	4.04		1.48	1.52		<2	

Remarks:
 Single underline denotes exceedance over Action Level.
 Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at C7 - Windsor House
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature		pH		Salinity		DO Saturation		DO		Turbidity		Suspended Solids	
					°C		-		ppt		%		mg/L		NTU		mg/L	
			m		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
28/12/2013	15:37	Fine	Middle	1.5	17.20	17.20	8.56	8.56	35.38	35.38	76.5	77.4	5.95	6.04	6.41	6.41	6	6.50
	15:39		Middle	1.5	17.20	17.20	8.55	8.55	35.57	35.57	78.3	78.6	6.10	6.12	6.41	6.42	7	
30/12/2013	14:46	Fine	Middle	1.5	17.60	17.60	8.56	8.56	35.08	35.08	78.0	78.9	6.04	6.08	3.30	3.30	4	3.50
	14:47		Middle	1.5	17.60	17.60	8.56	8.56	35.08	35.08	78.8	78.6	6.11	6.09	3.28	3.25	3	
2/1/2014	17:52	Cloudy	Middle	1.5	18.10	18.10	8.23	8.23	33.03	33.03	72.8	73.2	5.64	5.67	2.85	2.83	4	5.00
	17:53		Middle	1.5	18.10	18.10	8.23	8.23	33.08	33.08	73.1	71.4	5.64	5.58	2.79	2.81	6	
4/1/2014	10:59	Fine	Middle	1.5	17.80	17.80	8.39	8.39	34.81	34.81	66.8	67.2	5.15	5.19	4.30	4.30	2	2.00
	11:01		Middle	1.5	17.80	17.80	8.39	8.39	34.81	34.81	67.4	67.2	5.20	5.18	4.22	4.23	2	
6/1/2014	12:17	Fine	Middle	1.5	17.50	17.50	8.43	8.43	35.04	35.04	71.9	72.7	5.58	5.63	5.40	5.30	3	3.50
	12:19		Middle	1.5	17.50	17.50	8.43	8.43	35.04	35.04	72.8	72.3	5.64	5.60	5.30	5.24	4	
8/1/2014	12:20	Fine	Middle	1.5	18.40	18.40	8.40	8.40	35.06	35.06	72.4	73.3	5.51	5.57	4.90	4.95	5	5.00
	12:22		Middle	1.5	18.40	18.40	8.40	8.40	35.05	35.05	73.3	73.7	5.57	5.60	4.97	4.98	5	
10/1/2014	15:17	Cloudy	Middle	1.5	17.10	17.10	8.45	8.45	35.02	35.02	72.7	72.6	5.64	5.67	3.01	3.02	3	3.00
	15:19		Middle	1.5	17.10	17.10	8.44	8.44	35.02	35.02	72.6	72.5	5.67	5.65	3.06	3.08	3	
13/1/2014	15:07	Fine	Middle	1.5	17.10	17.10	8.45	8.45	34.85	34.85	70.5	71.2	5.51	5.56	2.14	2.14	4	3.50
	15:09		Middle	1.5	17.20	17.20	8.45	8.45	34.85	34.85	71.8	71.5	5.60	5.58	2.14	2.17	3	
15/1/2014	17:45	Fine	Middle	1.5	15.80	15.80	8.56	8.56	35.15	35.15	67.4	67.2	5.39	5.38	2.75	2.75	4	4.00
	17:47		Middle	1.5	15.80	15.80	8.56	8.56	35.16	35.16	66.5	66.6	5.32	5.33	2.74	2.71	4	
18/1/2014	10:12	Fine	Middle	1.5	16.20	16.20	8.48	8.48	34.79	34.79	64.9	65.3	5.17	5.20	2.31	2.31	3	3.00
	10:14		Middle	1.5	16.20	16.20	8.48	8.48	34.79	34.79	65.1	65.1	5.18	5.19	2.30	2.30	3	
20/1/2014	11:02	Fine	Middle	1.5	16.70	16.70	8.47	8.47	34.92	34.92	61.9	62.1	4.87	4.80	3.26	3.14	<2	<2
	11:04		Middle	1.5	16.20	16.20	8.47	8.47	34.92	34.92	62.1	62.0	4.88	4.87	3.13	3.11	<2	
22/1/2014	12:07	Fine	Middle	1.5	15.70	15.70	8.41	8.41	34.56	34.56	59.2	56.6	4.76	4.80	2.67	2.66	3	2.50
	12:09		Middle	1.5	15.70	15.70	8.40	8.40	34.56	34.56	59.9	60.0	4.82	4.82	2.65	2.61	2	
24/1/2014	12:23	Fine	Middle	1.5	16.40	16.40	8.42	8.42	34.69	34.69	62.4	62.9	4.95	4.99	2.66	2.61	3	3.00
	12:25		Middle	1.5	16.40	16.40	8.42	8.42	34.69	34.69	63.2	63.3	5.01	5.01	2.68	2.60	3	
27/1/2014	15:15	Fine	Middle	1.5	17.70	17.70	8.40	8.40	34.66	34.66	65.1	65.3	5.03	5.04	1.80	1.81	4	4.00
	15:17		Middle	1.5	17.80	17.80	8.39	8.39	34.66	34.66	65.6	65.4	5.06	5.05	1.83	1.83	4	

Remarks:
Single underline denotes exceedance over Action Level.
Double underline denotes exceedance over Limit Level.



Water Monitoring Result at C7 - Windsor House
Mid-Ebb Tide

Date	Time	Weater Condition	Sampling Depth		Water Temperature			pH			Salinity			DO Saturation			DO			Turbidity			Suspended Solids	
					°C			-			ppt			%			mg/L			NTU			mg/L	
			m		Value	Average		Value	Average		Value	Average		Value	Average		Value	Average		Value	Average		Value	Average
28/12/2013	19:53	Fine	Middle	2	15.10	15.10	15.10	8.27	8.27	8.27	32.80	32.80	32.81	68.7	69.2	69.0	5.66	5.70	5.68	4.81	4.78	4.83	6	5.50
	19:54		Middle	2	15.10	15.10		8.27	8.27		32.81	32.81		69.1	68.8		5.69	5.66		4.87	4.85		5	
30/12/2013	1:00	Fine	Middle	1	15.80	15.80	15.80	8.33	8.33	8.33	30.79	30.81	30.81	58.9	59.1	59.0	4.85	4.86	4.85	3.26	3.33	3.32	3	2.50
	1:01		Middle	1	15.80	15.80		8.32	8.32		30.82	30.82		59.0	58.9		4.85	4.84		3.28	3.39		2	
2/1/2014	14:57	Fine	Middle	2	18.30	18.30	18.35	8.45	8.45	8.45	35.67	35.67	35.67	73.3	73.9	74.0	5.57	5.60	5.62	3.36	3.42	3.37	2	2.00
	14:59		Middle	2	18.40	18.40		8.45	8.45		35.67	35.67		74.4	74.3		5.65	5.64		3.37	3.33		2	
4/1/2014	15:02	Fine	Middle	2	18.80	18.80	18.80	8.40	8.40	8.40	35.31	35.31	35.31	69.8	71.1	71.0	5.28	5.38	5.37	3.67	3.68	3.66	3	4.00
	15:04		Middle	2	18.80	18.80		8.40	8.40		35.30	35.30		71.3	71.6		5.39	5.41		3.66	3.64		5	
6/1/2014	15:55	Fine	Middle	2	17.60	17.60	17.60	8.44	8.44	8.44	35.39	35.39	35.39	77.6	77.9	77.9	5.98	6.00	6.00	4.64	4.63	4.65	5	5.50
	15:57		Middle	2	17.60	17.60		8.44	8.44		35.38	35.38		78.0	78.2		6.00	6.01		4.62	4.69		6	
8/1/2014	20:07	Cloudy	Middle	1	18.00	18.00	18.03	7.87	7.87	7.87	33.54	33.53	33.53	66.9	66.6	66.7	5.18	5.15	5.16	1.50	1.46	1.45	2	3.00
	20:08		Middle	1	18.10	18.00		7.87	7.87		33.53	33.53		66.6	66.5		5.15	5.14		1.44	1.40		4	
10/1/2014	19:57	Cloudy	Middle	2	16.70	16.70	16.70	7.97	7.97	7.97	33.64	33.64	33.64	86.0	86.0	86.1	6.83	6.83	6.84	3.79	3.89	3.87	3	2.50
	19:58		Middle	2	16.70	16.70		7.96	7.96		33.64	33.64		86.1	86.1		6.84	6.84		3.94	3.86		2	
13/1/2014	0:59	Cloudy	Middle	1	14.30	14.30	14.30	7.98	7.98	7.97	32.41	32.41	32.41	68.6	68.3	67.7	5.76	5.73	5.70	1.51	1.49	1.50	2	2.50
	1:00		Middle	1	14.30	14.30		7.96	7.96		32.40	32.40		67.0	66.8		5.72	5.60		1.53	1.46		3	
16/1/2014	2:15	Fine	Middle	1	14.00	14.00	14.00	8.06	8.06	8.05	32.33	32.33	32.33	73.3	72.1	72.3	6.02	6.10	6.07	1.84	1.89	1.84	3	3.00
	2:16		Middle	1	14.00	14.00		8.04	8.04		32.32	32.32		71.9	71.7		6.08	6.06		1.82	1.79		3	
18/1/2014	2:28	Fine	Middle	1	15.50	15.50	15.50	8.07	8.07	8.06	31.59	31.58	31.57	59.9	59.5	59.5	4.93	4.90	4.87	1.88	1.86	1.85	3	3.50
	2:29		Middle	1	15.50	15.50		8.05	8.05		31.55	31.55		58.6	59.8		4.82	4.84		1.84	1.80		4	
20/1/2014	15:02	Fine	Middle	2	17.70	17.70	17.70	8.43	8.43	8.43	34.98	34.98	34.98	65.8	66.6	67.0	5.07	5.15	5.16	2.57	2.59	2.59	<2	<2
	15:04		Middle	2	17.70	17.70		8.43	8.43		34.98	34.98		67.4	68.3		5.17	5.25		2.59	2.60		<2	
22/1/2014	15:32	Fine	Middle	2	16.00	16.00	16.00	8.42	8.42	8.42	34.39	34.39	34.39	62.4	63.0	63.1	4.99	5.05	5.06	1.71	1.71	1.71	3	3.00
	15:34		Middle	2	16.00	16.00		8.42	8.42		34.39	34.39		63.5	63.6		5.09	5.09		1.71	1.70		3	
24/1/2014	19:17	Fine	Middle	1	17.30	17.30	17.30	8.16	8.16	8.16	31.29	31.29	31.29	82.1	82.0	82.0	6.52	6.52	6.52	2.29	2.72	2.40	3	2.50
	19:18		Middle	1	17.30	17.30		8.16	8.16		31.29	31.29		81.8	82.0		6.50	6.52		2.27	2.30		2	
27/1/2014	20:33	Fine	Middle	2	17.50	17.50	17.45	8.21	8.21	8.20	31.67	31.67	31.67	86.3	86.0	86.1	6.83	6.81	6.81	1.04	1.07	1.08	3	3.50
	20:34		Middle	2	17.40	17.40		8.19	8.20		31.67	31.67		86.1	85.8		6.81	6.80		1.08	1.11		4	

Remarks:
Single underline denotes exceedance over Action Level.
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at C7 - Windsor House
Mid-Flood Tide**

Date	Time	Weater Condition	Sampling Depth		Water Temperature		pH		Salinity		DO Saturation		DO		Turbidity		Suspended Solids							
			m		°C		-		ppt		%		mg/L		NTU		mg/L							
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average						
29/1/2014	15:17	Fine	Middle	1.5	18.50	18.50	18.50	8.44	8.44	8.44	34.59	34.59	34.59	71.7	72.0	71.9	5.45	5.48	5.48	1.52	1.54	1.55	2	2.00
	15:19		Middle	1.5	18.50	18.50		8.44	8.44		34.59	34.59		72.0	71.9		5.48	5.49		1.57	1.58		2	
4/2/2014	11:36	Fine	Middle	1.5	18.10	18.10	18.10	8.51	8.51	8.51	34.14	34.14	34.14	68.9	69.0	69.1	5.30	5.31	5.32	3.11	3.11	3.12	2	2.50
	11:38		Middle	1.5	18.10	18.10		8.50	8.50		34.14	34.14		68.8	69.6		5.29	5.36		3.12	3.12		3	
6/2/2014	12:43	Fine	Middle	1.5	19.10	19.10	19.15	8.51	8.51	8.51	34.91	34.91	34.90	67.7	67.5	67.1	5.09	5.07	5.04	2.03	2.02	2.01	7	7.00
	12:45		Middle	1.5	19.20	19.20		8.51	8.51		34.89	34.89		66.9	66.1		5.02	4.97		2.00	1.98		7	
8/2/2014	13:56	Fine	Middle	1.5	18.20	18.20	18.20	8.42	8.42	8.42	34.19	34.19	34.19	56.8	57.0	57.1	4.37	4.38	4.39	0.81	0.81	0.80	4	4.00
	13:58		Middle	1.5	18.20	18.20		8.42	8.42		34.19	34.19		57.2	57.2		4.39	4.40		0.80	0.79		4	
10/2/2014	12:32	Fine	Middle	1.5	15.90	15.90	15.85	8.52	8.52	8.52	34.41	34.41	34.42	60.9	60.6	60.7	4.89	4.87	4.87	1.48	1.49	1.49	3	3.00
	12:34		Middle	1.5	15.80	15.80		8.51	8.51		34.43	34.43		60.6	60.6		4.87	4.86		1.50	1.50		3	
12/2/2014	14:45	Cloudy	Middle	1.5	15.40	15.40	15.35	8.51	8.51	8.51	34.72	34.72	34.72	59.9	60.7	60.7	4.85	4.91	4.91	3.72	3.73	3.75	5	5.50
	14:47		Middle	1.5	15.30	15.30		8.50	8.50		34.72	34.72		61.0	61.0		4.94	4.94		3.75	3.78		6	
14/2/2014	17:48	Fine	Middle	1.5	16.00	16.00	16.00	8.54	8.54	8.54	34.82	34.82	34.82	63.5	63.7	63.7	5.08	5.09	5.09	1.81	1.82	1.83	4	4.00
	17:50		Middle	1.5	16.00	16.00		8.53	8.53		34.82	34.82		63.7	63.8		5.09	5.09		1.83	1.85		4	
17/2/2014	19:52	Cloudy	Middle	1.5	18.80	18.80	18.80	8.07	8.07	8.07	31.77	31.77	31.79	65.9	66.3	65.6	5.07	5.09	5.04	1.04	1.06	1.09	3	2.50
	19:53		Middle	1.5	18.80	18.80		8.07	8.07		31.80	31.80		65.4	64.6		5.03	4.96		1.17	1.08		2	
19/2/2014	11:22	Cloudy	Middle	1.5	14.50	14.50	14.60	8.37	8.37	8.37	35.00	35.00	35.00	58.2	58.6	58.7	4.76	4.80	4.80	3.21	3.21	3.23	3	3.00
	11:24		Middle	1.5	14.70	14.70		8.36	8.36		35.00	35.00		58.8	59.0		4.82	4.83		3.23	3.27		3	
21/2/2014	12:02	Fine	Middle	1.5	16.30	16.30	16.35	8.41	8.41	8.41	35.21	35.21	35.21	58.7	58.7	58.8	4.65	4.64	4.65	1.00	1.00	1.00	3	2.50
	12:04		Middle	1.5	16.40	16.40		8.40	8.40		35.21	35.21		58.8	58.9		4.65	4.66		1.00	1.00		2	
24/2/2014	14:17	Fine	Middle	1.5	17.40	17.40	17.45	8.50	8.50	8.50	35.55	35.55	35.55	73.6	73.5	73.7	5.69	5.68	5.66	1.51	1.51	1.52	3	2.50
	14:19		Middle	1.5	17.50	17.50		8.49	8.49		35.55	35.55		75.0	72.6		5.64	5.61		1.52	1.54		2	
26/2/2014	15:25	Fine	Middle	1.5	18.30	18.30	18.35	8.44	8.44	8.44	35.31	35.31	35.31	68.1	68.4	68.5	5.19	6.21	5.46	2.73	2.72	2.72	2	2.50
	15:27		Middle	1.5	18.40	18.40		8.44	8.44		35.31	35.31		68.6	68.7		5.22	5.22		2.72	2.72		3	

Remarks:
Single underline denotes exceedance over Action Level.
Double underline denotes exceedance over Limit Level.






Water Monitoring Result at C7 - Windsor House
Mid-Ebb Tide

Date	Time	Weater Condition	Sampling Depth		Water Temperature		pH		Salinity		DO Saturation		DO		Turbidity		Suspended Solids							
					°C		-		ppt		%		mg/L		NTU		mg/L							
			m	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average							
29/1/2014	1:00	Fine	Middle	1	16.90	16.90	16.93	8.20	8.20	8.19	30.51	30.51	30.51	70.6	71.6	71.2	5.68	5.76	5.72	1.87	1.90	1.89	3	3.00
	1:01		Middle	1	17.00	16.90		8.18	8.18		30.51	30.51		71.7	70.8		5.76	5.69		1.84	1.93		3	
4/2/2014	16:09	Fine	Middle	2	18.20	18.20	18.20	8.47	8.47	8.47	34.10	34.10	34.09	74.2	75.6	74.7	5.70	5.81	5.74	1.38	1.37	1.37	3	3.00
	16:11		Middle	2	18.20	18.20		8.47	8.47		34.08	34.08		75.1	74.0		5.77	5.69		1.36	1.35		3	
6/2/2014	17:30	Fine	Middle	2	18.80	18.80	18.85	8.52	8.52	8.52	34.97	34.97	34.97	72.1	72.7	73.0	5.44	5.49	5.51	0.88	0.90	0.90	4	3.50
	17:32		Middle	2	18.90	18.90		8.52	8.52		34.97	34.97		73.7	73.6		5.57	5.55		0.91	0.92		3	
8/2/2014	22:23	Cloudy	Middle	1	18.00	18.00	18.00	8.23	8.23	8.22	30.75	30.75	30.75	76.4	77.3	76.5	6.01	6.08	6.03	1.07	1.10	1.09	4	4.00
	22:24		Middle	1	18.00	18.00		8.21	8.21		30.75	30.75		76.4	76.0		6.01	6.00		1.08	1.12		4	
10/2/2014	23:58	Cloudy	Middle	1	13.00	13.00	13.00	8.24	8.24	8.23	28.78	28.78	28.79	57.9	58.3	58.2	5.10	5.15	5.14	2.62	2.65	2.60	2	2.50
	23:59		Middle	1	13.00	13.00		8.21	8.21		28.79	28.79		58.1	58.5		5.13	5.16		2.58	2.55		3	
12/2/2014	1:07	Cloudy	Middle	1	13.50	13.50	13.50	8.25	8.25	8.25	28.17	28.17	28.16	56.5	56.7	56.5	4.95	4.96	4.95	4.13	4.20	4.17	8	8.00
	1:08		Middle	1	13.50	13.50		8.24	8.24		28.15	28.15		56.5	56.3		4.94	4.93		4.16	4.18		8	
15/2/2014	2:40	Cloudy	Middle	1	13.90	13.90	13.90	7.99	7.99	7.99	27.68	27.69	27.69	50.6	50.6	50.7	4.41	4.41	4.42	3.01	3.04	3.08	2	2.50
	2:41		Middle	1	13.90	13.90		7.99	7.99		27.70	27.70		50.8	50.8		4.42	4.43		3.16	3.10		3	
17/2/2014	14:32	Cloudy	Middle	2	18.30	18.30	18.40	8.41	8.41	8.41	34.87	34.87	34.87	72.0	72.4	72.3	5.49	5.52	5.51	1.51	1.52	1.51	<2	<2
	14:34		Middle	2	18.50	18.50		8.41	8.41		34.87	34.87		72.6	72.3		5.53	5.51		1.51	1.51		<2	
19/2/2014	14:47	Cloudy	Middle	2	15.30	15.30	15.25	8.40	8.40	8.40	34.77	34.77	34.77	61.3	61.8	61.9	4.98	5.02	5.03	1.51	1.51	1.52	2	2.50
	14:49		Middle	2	15.20	15.20		8.40	8.40		34.77	34.77		62.1	62.3		5.05	5.06		1.52	1.52		3	
21/2/2014	15:17	Fine	Middle	2	16.80	16.80	16.80	8.39	8.39	8.39	35.20	35.20	35.20	64.8	65.5	65.4	5.13	5.17	5.16	1.93	1.95	1.97	3	3.00
	15:19		Middle	2	16.80	16.80		8.39	8.39		35.20	35.20		65.7	65.4		5.18	5.16		1.98	2.00		3	
24/2/2014	18:20	Cloudy	Middle	2	17.90	17.90	17.90	8.07	8.07	8.08	32.42	32.42	32.42	72.5	73.2	72.7	5.67	5.72	5.68	1.01	1.03	1.04	3	3.00
	18:21		Middle	2	17.90	17.90		8.08	8.08		32.42	32.42		72.5	72.4		5.67	5.66		1.05	1.07		3	
26/2/2014	23:26	Cloudy	Middle	1	18.70	18.70	18.70	8.21	8.20	8.20	30.70	30.71	30.70	59.7	60.9	60.8	4.63	4.73	4.72	1.78	1.76	1.72	4	4.00
	23:27		Middle	1	18.70	18.70		8.20	8.20		30.70	30.70		61.3	61.1		4.76	4.74		1.70	1.64		4	

Remarks:
Single underline denotes exceedance over Action Level.
Double underline denotes exceedance over Limit Level.



Graphic Presentation of Water Quality Result of C7 - Windsor House

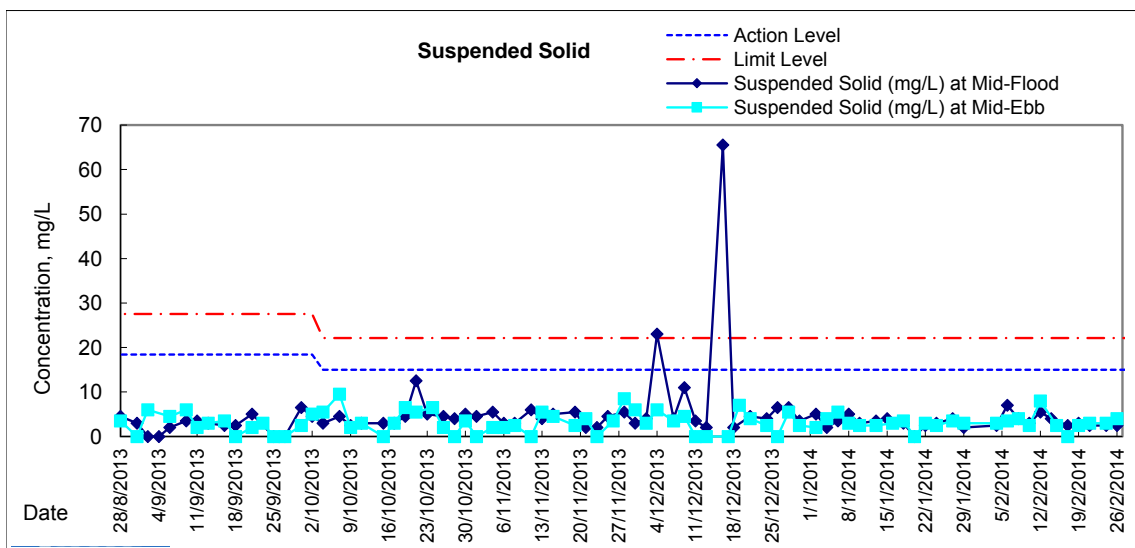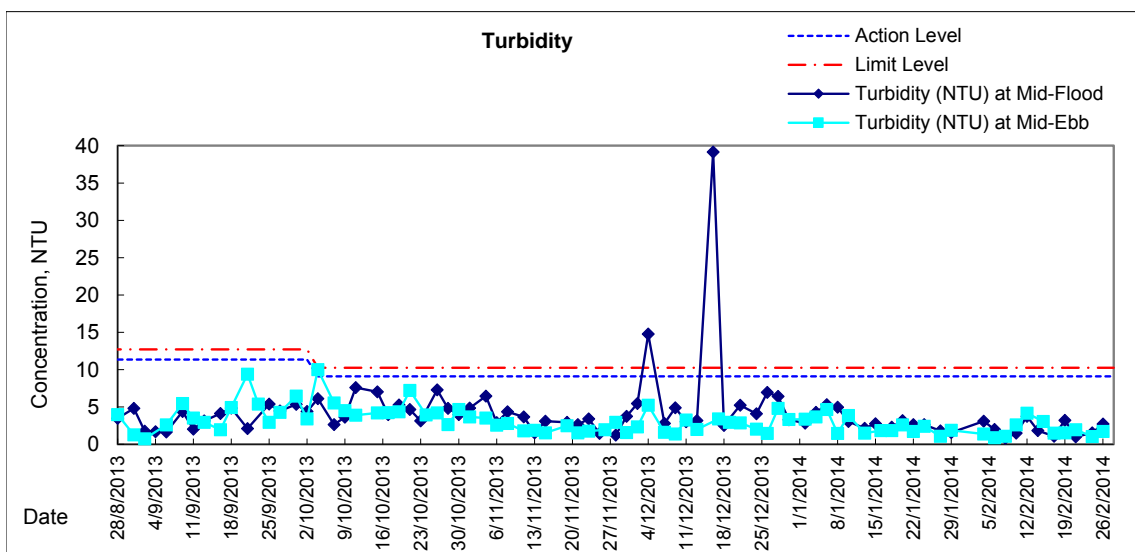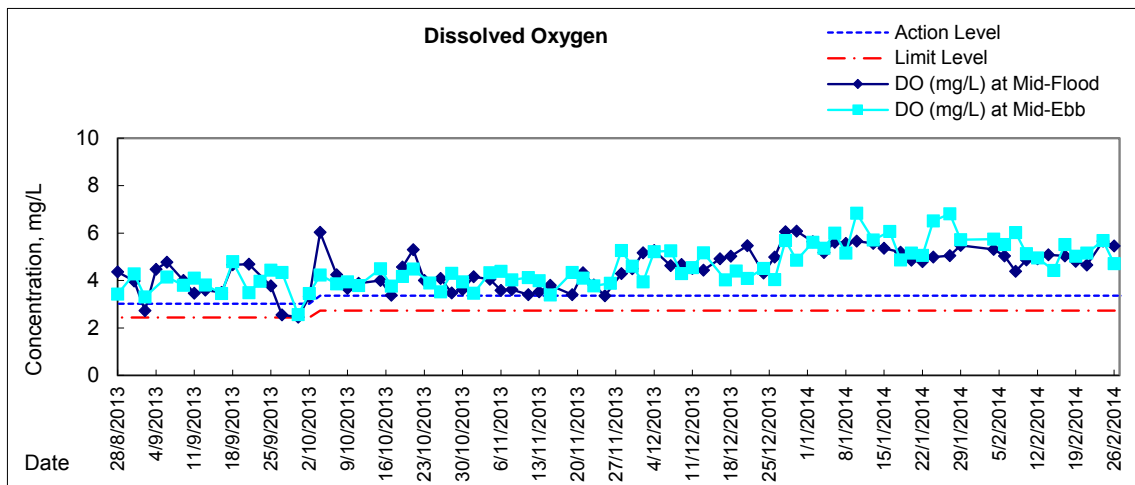



Appendix 5.1

Event Action Plans



Lam Geotechnics Limited

Contract No. HK/2011/07
Wanchai Development Phase II and Central Wanchai Bypass
(Shatin to Central Link (SCL) Protection
Works at Causeway Bay Typhoon Shelter)

Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level	<ol style="list-style-type: none"> 1. Notify IEC, ER and Contactor 2. Carry out investigation 3. Report the results of investigation to the IEC, ER and Contactor 4. Discuss with the IEC and Contractor on remedial measures required 5. Increase monitoring frequency to check mitigation effectiveness <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none"> 1. Review the investigation results submitted by the ET 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly 3. Advise the ER on the effectiveness of the proposed remedial measures <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing 2. Notify Contractor 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented 4. Supervise the implementation of remedial measures <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC and ER 2. Implement noise mitigation proposals <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>
Limit Level	<ol style="list-style-type: none"> 1. Inform IEC, ER, EPD and Contractor 2. Repeat measurement to confirm findings 3. Increase monitoring frequency 4. Identify source and investigate the cause of exceedance 5. Carry out analysis of Contractor's working procedures. Discuss with the IEC, Contractor and ER on remedial measures require 6. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results 7. If exceedance stops, cease additional monitoring <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET and Contractor on the potential remedial actions 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing 2. Notify Contractor 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented 4. Supervise the implementation of remedial measures 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification 3. Implement the agreed proposals 4. Submit further proposal if problem still not under control 5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>



Lam Geotechnics Limited

Contract No. HK/2011/07

Wanchai Development Phase II and Central Wanchai Bypass
(Shatin to Central Link (SCL) Protection
Works at Causeway Bay Typhoon Shelter)

Event / Action Plan for Construction Air Quality

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
ACTION LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of complaint and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Notify Contractor. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified.)
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Submit proposals for remedial to ER within three working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified.)
LIMIT LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC, ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within three working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified.)



Lam Geotechnics Limited

Contract No. HK/2011/07

Wanchai Development Phase II and Central Wanchai Bypass

(Shatin to Central Link (SCL) Protection

Works at Causeway Bay Typhoon Shelter)

2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none">1. Notify IEC, ER, Contractor and EPD;2. Identify source;3. Repeat measurement to confirm findings;4. Increase monitoring frequency to daily;5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken;7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;8. If exceedance stops, cease additional monitoring. <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none">1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;3. Supervise the implementation of remedial measures. <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none">1. Confirm receipt of notification of failure in writing;2. Notify Contractor;3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented;4. Ensure remedial measures properly implemented;5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none">1. Take immediate action to avoid further exceedance;2. Submit proposals for remedial actions to IEC within three working days of notification;3. Implement the agreed proposals;4. Resubmit proposals if problem still not under control;5. Stop the relevant portion of works as determined by the ER until the exceedance is abated. <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>
---	--	---	---	--



Event and Action Plan for Marine Water Quality

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Action level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next working day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Limit level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures; As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities. (The above actions should be taken within 1 working day after the exceedance is identified)



Appendix 6.1

Complaints Log



Lam Geotechnics Limited

Contract No. HK/2011/07
Wanchai Development Phase II and Central Wanchai Bypass
(Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter)

Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
--	--	--	--	--	--	--



Appendix 6.2

Notification of Exceedances



Ref no.	Date	Tidal	Location	Parameters (Unit)	Measured	Action Level	Limit Level	Follow-up action	
X_10C602	04-Dec-13	Mid-flood	C7	DO(mg/L)	5.26	3.36	2.73	Possible reason:	Natural variation or changes of water quality in the vicinity of the water quality monitoring station.
				Turbidity	14.76	9.10	10.25	Action taken / to be taken:	Immediate repeated in-situ measurements had conducted to confirm the exceedances. Checking with contractor's works. Checking with contractor's inspection record.
				SS	23.00	15.00	22.13	Remarks / Other Obs:	Silt screen was in proper condition. Installation of rebar for EVA at Eastern Breakwater and dredging of type 2 marine sediment was conducted by contractor HY/2009/15 on that day. Mitigation measure including frame type silt curtain was confirmed in place. In view of no further exceedance was recorded in the next consecutive monitoring despite on-going marine works within same sampling date. The exceedance was considered as works-related.
X_10C603	16-Dec-13	Mid-flood	C7	DO(mg/L)	4.91	3.36	2.73	Possible reason:	Underwater silt screen inspection leading to changes of water quality in the vicinity of the water quality monitoring station.
				Turbidity	39.13	9.10	10.25	Action taken / to be taken:	Immediate repeated in-situ measurements had conducted to confirm the exceedances. Checking with contractor's works.
				SS	62.50	15.00	22.13	Remarks / Other Obs:	Underwater silt screen inspection was observed during water quality monitoring. According to on-site observation during sampling, it was considered that the dragging action of unwinding silt curtain installed around the silt screen could have impaired the water quality and lead to the abnormal turbidity and SS level. Contractor was advised to review the underwater silt screen inspection process as a propose to reduce the impact on water quality in the vicinity of water quality monitoring station. In view of no further exceedance was recorded in the next consecutive monitoring despite on-going marine works within same sampling date. The exceedance was considered as works-related.



Appendix 7.1

Construction Programme

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	2014				2015				2016							
									Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4			
OHVD Slab and Cable Trough Construction																								
S3_5075	Demolish bulkhead wall between TS1 & TS2	7d/wk-1	47d	24-Feb-14	12-Apr-14	14-Jan-14	04-Mar-14	-38d	■ Demolish bulkhead wall between TS1 & TS2															
S3_5080	TS2 - OHVD slab (access through temp. opening at CCT in Portion 6&22)	7d/wk-1	90d	13-Apr-14	18-Jul-14	05-Mar-14	09-Jun-14	-38d	■ TS2 - OHVD slab (access through temp. opening at CCT in Portion 6&22)															
S3_6210	TS2 - cable trough (access through temp. opening at CCT in Portion 6&22)	7d/wk-1	90d	13-Apr-14	18-Jul-14	05-Mar-14	09-Jun-14	-38d	■ TS2 - cable trough (access through temp. opening at CCT in Portion 6&22)															
S1_5855	Make good temporary access shaft and complete remaining OHVD at TS1(Portion 1,2,6,22)	7d/wk-1	24d	19-Jul-14	11-Aug-14	10-Jun-14	04-Jul-14	-38d	■ Make good temporary access shaft and complete remaining OHVD at TS1(Portion 1,2,6,22)															
S3_6212	Completion of Section 3 - TS1/TS2 Area (below -6mpd) KD8)	7d/wk-2	0d		11-Aug-14		04-Jul-14	-38d	◆ Completion of Section 3 - TS1/TS2 Area (below -6mpd) KD8)															
Works in TS4/ME4 Area (Portion 14A, 14B, 15, 23)																								
TS4/ME4 - ELS Works & Rock Excavation																								
TS4/ME4- West Portion Rock Excavation + Pipe Roofing Installation																								
S27155	WB Area Rock excavation -25 up to -35mPD	7d/wk-1	28d	17-Jul-13 A	25-Oct-13	17-Apr-13	24-Apr-13	-177d	■ WB Area Rock excavation -25 up to -35mPD															
TS4/ME4 - Mined Tunnel East Portal Works																								
WB Tunnel																								
S27115	WB - short portion CCT (base slab, Wall and Strut) to facilitate SR8 excavation (-35mPD)	7d/wk-1	20d	26-Oct-13	14-Nov-13	25-Apr-13	15-May-13	-177d	■ WB - short portion CCT (base slab, Wall and Strut) to facilitate SR8 excavation (-35mPD)															
S27100	WB Mined Tunnel "Heading/Bench" Excavation - 3.5 (Arch rib->Mining->Shotcrete)	7d/wk-1	24d	15-Nov-13	08-Dec-13	16-May-13	09-Jun-13	-177d	■ WB Mined Tunnel "Heading/Bench" Excavation - 3.5 (Arch rib->Mining->Shotcrete)															
S27105	WB Tunnel Lining (base slab & kicker and erect shutter then Lining) - 1.5m	7d/wk-1	21d	06-Dec-13	28-Dec-13	07-Jun-13	28-Jun-13	-177d	■ WB Tunnel Lining (base slab & kicker and erect shutter then Lining) - 1.5m															
EB Tunnel																								
S27085	EB Mined Tunnel "Outer/Inner" Excavation - 4.5m (Arch rib->Mining->Shotcrete)	7d/wk-1	31d	16-Aug-13 A	21-Oct-13	04-Jun-13	07-Jun-13	-131d	■ EB Mined Tunnel "Outer/Inner" Excavation - 4.5m (Arch rib->Mining->Shotcrete)															
S27095	EB Tunnel Base Slab + Arc Concrete lining - 2.5m	7d/wk-1	21d	21-Oct-13	10-Nov-13	07-Jun-13	28-Jun-13	-131d	■ EB Tunnel Base Slab + Arc Concrete lining - 2.5m															
SR8 Tunnel																								
S27070	SR8 Mined Tunnel Full Face Excavation - 5m (Arch rib->Mining->Shotcrete)	7d/wk-1	21d	15-Nov-13	05-Dec-13	16-May-13	06-Jun-13	-177d	■ SR8 Mined Tunnel Full Face Excavation - 5m (Arch rib->Mining->Shotcrete)															
S5_54712	SR8 Tunnel Base Slab + Arc Concrete lining - 1st 5m	7d/wk-1	21d	06-Dec-13	28-Dec-13	07-Jun-13	28-Jun-13	-177d	■ SR8 Tunnel Base Slab + Arc Concrete lining - 1st 5m															
TS4/ME4 - CCT RC Structure																								
CCT - Area A																								
S26820	TS4 Construct tunnel wall & OHVD + Roof slab	7d/wk-1	36d	14-Jun-13 A	04-Nov-13*	20-May-13	06-Jun-13	-146d	■ TS4 Construct tunnel wall & OHVD + Roof slab															
S5_59785	Waterproofing on top of completed CCT box (incl. screeding) & mass concrete infill	7d/wk-1	12d	05-Nov-13	16-Nov-13	07-Jun-13	19-Jun-13	-146d	■ Waterproofing on top of completed CCT box (incl. screeding) & mass concrete infill															
S5_59820	Construct access shaft at TZ4	7d/wk-1	36d	05-Nov-13	10-Dec-13	26-Jul-13	30-Aug-13	-99d	■ Construct access shaft at TZ4															
S5_59795	King Post Load Transfer - CWB top slab area A	7d/wk-1	12d	17-Nov-13	28-Nov-13	20-Jun-13	02-Jul-13	-146d	■ King Post Load Transfer - CWB top slab area A															
CCT - Area B																								
S26765	TS4 Construct tunnel base slab	7d/wk-1	24d	18-Oct-13*	10-Nov-13	18-Apr-13	12-May-13	-176d	■ TS4 Construct tunnel base slab															

Remaining Work

◆

Remaining Work

Critical Remaining Work

◆

Milestone

Summary

Summary

3 of 13

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. J

Date

18-Oct-13

Revision

1ST Submission

Checked

Approved

KC

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	2014				2015				2016				
									Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
S26770	TS4 Construct tunnel wall & OHVD + Roof slab	7d/wk-1	36d	30-Oct-13*	04-Dec-13*	30-Apr-13	06-Jun-13	-176d	<div></div>	TS4 Construct tunnel wall & OHVD + Roof slab											
S26785	Waterproofing on top of completed CCT box (incl. screeding) & mass concrete infill	7d/wk-1	12d	05-Dec-13	16-Dec-13	07-Jun-13	19-Jun-13	-176d	<div></div>	Waterproofing on top of completed CCT box (incl. screeding) & mass concrete infill											
S5_59800	King Post Load Transfer - CWB top slab area B	7d/wk-1	12d	17-Dec-13	30-Dec-13	20-Jun-13	02-Jul-13	-176d	<div></div>	King Post Load Transfer - CWB top slab area B											
Stitching - CCT Area C																					
S26830	EB - CCT stitching (, base slab, wall & roof)	7d/wk-1	36d	05-Nov-13	10-Dec-13	23-Jun-13	29-Jul-13	-131d	<div></div>	EB - CCT stitching (, base slab, wall & roof)											
S26825	WB - CCT stitching (, base slab, wall & roof)	7d/wk-1	36d	21-Dec-13	28-Jan-14	23-Jun-13	29-Jul-13	-177d	<div></div>	WB - CCT stitching (, base slab, wall & roof)											
S26835	SR8 - CCT stitching (, base slab, wall & roof)	7d/wk-1	36d	21-Dec-13	28-Jan-14	23-Jun-13	29-Jul-13	-177d	<div></div>	SR8 - CCT stitching (, base slab, wall & roof)											
S5_59780	Waterproofing on top of completed CCT box (incl. screeding) & mass concrete infill	7d/wk-1	4d	28-Jan-14	02-Feb-14	29-Jul-13	01-Aug-13	-177d	<div></div>	Waterproofing on top of completed CCT box (incl. screeding) & mass concrete infill											
S5_59805	King Post Load Transfer - CWB top slab area C	7d/wk-1	4d	30-Jan-14	05-Feb-14	31-Jul-13	03-Aug-13	-177d	<div></div>	King Post Load Transfer - CWB top slab area C											
SCL CCT RC Structure -Area A & B																					
S26775	Rockfill to underside of SCL tunnel / soil backfill in other areas	7d/wk-1	6d	31-Dec-13	06-Jan-14	03-Jul-13	08-Jul-13	-176d	<div></div>	Rockfill to underside of SCL tunnel / soil backfill in other areas											
S26745	ME4 - remove strut and construct SCL tunnel base slab	7d/wk-1	24d	07-Jan-14	30-Jan-14	09-Jul-13	01-Aug-13	-176d	<div></div>	ME4 - remove strut and construct SCL tunnel base slab											
S26750	ME4 - SCL tunnel, wall and roof slab (incl. removal of L4 struts & backfilling works)	7d/wk-1	36d	17-Jan-14	24-Feb-14	19-Jul-13	23-Aug-13	-176d	<div></div>	ME4 - SCL tunnel, wall and roof slab (incl. removal of L4 struts & backfilling works)											
S26760	Waterproofing on top of completed CCT box (incl. screeding)	7d/wk-1	6d	24-Feb-14	01-Mar-14	23-Aug-13	28-Aug-13	-176d	<div></div>	Waterproofing on top of completed CCT box (incl. screeding)											
S5_59810	King Post Load Transfer - SCL top slab area	7d/wk-1	6d	26-Feb-14	03-Mar-14	25-Aug-13	30-Aug-13	-176d	<div></div>	King Post Load Transfer - SCL top slab area											
SCL CCT RC Structure - Area C																					
S5_59755	Rockfill to underside of SCL tunnel / soil backfill in other areas	7d/wk-1	2d	06-Feb-14	07-Feb-14	04-Aug-13	05-Aug-13	-177d	<div></div>	Rockfill to underside of SCL tunnel / soil backfill in other areas											
S5_59760	ME4 - remove strut and construct SCL tunnel base slab	7d/wk-1	6d	08-Feb-14	13-Feb-14	06-Aug-13	11-Aug-13	-177d	<div></div>	ME4 - remove strut and construct SCL tunnel base slab											
S5_59765	ME4 - SCL tunnel, wall and roof slab (incl. removal of L4 struts & backfilling works)	7d/wk-1	12d	14-Feb-14	25-Feb-14	12-Aug-13	23-Aug-13	-177d	<div></div>	ME4 - SCL tunnel, wall and roof slab (incl. removal of L4 struts & backfilling works)											
S5_59825	Construct access shaft at TZ6	7d/wk-1	6d	26-Feb-14	03-Mar-14	25-Aug-13	30-Aug-13	-176d	<div></div>	Construct access shaft at TZ6											
S5_59775	Waterproofing on top of completed CCT box (incl. screeding)	7d/wk-1	3d	28-Feb-14	02-Mar-14	26-Aug-13	28-Aug-13	-177d	<div></div>	Waterproofing on top of completed CCT box (incl. screeding)											
S5_59790	King Post Load Transfer - SCL top slab area	7d/wk-1	3d	02-Mar-14	04-Mar-14	28-Aug-13	30-Aug-13	-177d	<div></div>	King Post Load Transfer - SCL top slab area											
TS4/ME4 - Removal of Temporary Reclamation																					
TS4/ME4, Removal of Temporary Reclamation																					
S62755	Remaining backfilling works to sea bed level, -6mPD (TS4/ME4 Area)	7d/wk-1	6d	05-Mar-14	10-Mar-14	31-Aug-13	05-Sep-13	-177d	<div></div>	Remaining backfilling works to sea bed level, -6mPD (TS4/ME4 Area)											
S5_59815	Reinstatement of vertical seawall	7d/wk-1	6d	05-Mar-14	10-Mar-14	31-Aug-13	05-Sep-13	-177d	<div></div>	Reinstatement of vertical seawall											
S26880	Recharge water inside cofferdam concurrent with removal of strut L1 & L2	7d/wk-1	6d	11-Mar-14	16-Mar-14	06-Sep-13	11-Sep-13	-177d	<div></div>	Recharge water inside cofferdam concurrent with removal of strut L1 & L2											
S26845	Remove general fill /sea wall block south side	7d/wk-1	17d	13-Mar-14	29-Mar-14	08-Sep-13	25-Sep-13	-177d	<div></div>	Remove general fill /sea wall block south side											
S26865	Saw cut diaphragm wall (nos.) - south side	7d/wk-1	25d	25-Mar-14	22-Apr-14	21-Sep-13	17-Oct-13	-177d	<div></div>	Saw cut diaphragm wall (nos.) - south side											

Remaining Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Summay

4 of 13

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. J

Date

18-Oct-13

Revision

1ST Submission

Checked

Approved

KC

Activity ID		Activity Name	Calendar	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	2014				2015				2016					
										Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
S5_54717		Remove seawall block/general fill - north side	7d/wk-1	17d	23-Apr-14	11-May-14	18-Oct-13	03-Nov-13	-177d			■ Remove seawall block/general fill - north side											
S26855		Form TZ6	7d/wk-1	18d	23-Apr-14	12-May-14	06-Nov-13	23-Nov-13	-158d			■ Form TZ6											
S5_54722		Saw cut diaphragm wall (nos.) - north side	7d/wk-1	25d	07-May-14	31-May-14	30-Oct-13	23-Nov-13	-177d			■ Saw cut diaphragm wall (nos.) - north side											
S26860		Form TZ4	7d/wk-1	18d	14-May-14	31-May-14	06-Nov-13	23-Nov-13	-177d			■ Form TZ4											
S26875		Completion of Section 2 (With ME4 option) (KD7)	7d/wk-1	0d		31-May-14*		23-Nov-13	-177d			◆ Completion of Section 2 (With ME4 option) (KD7)											
S26890		Completion of Section 7B (ME4) (KD13)	7d/wk-1	0d		31-May-14*		23-Nov-13	-177d			◆ Completion of Section 7B (ME4) (KD13)											
Re-Provision of Permanent Jetty & Floating Pontoon																							
Re-Provision of Permanent Jetty & Floating Pontoon																							
S6_5258		Provision of Temporary Jetty (Mobile Crane) (until permanent re-provision is completed)	6d/wk	160d	07-May-14	14-Nov-14	20-Jul-15	27-Jan-16	357d			■ Provision of Temporary Jetty (Mobile Crane) (until permanent re-provision is completed)											
S6_5260		Re-provision of permanent jetty and floating pontoon	6d/wk	72d	03-Jun-14	26-Aug-14	19-Oct-15	13-Jan-16	411d			■ Re-provision of permanent jetty and floating pontoon											
S6_5265		Re-provision of permanent jetty and floating pontoon - RHKYC Inspection / Appvl	6d/wk	12d	01-Nov-14	14-Nov-14	14-Jan-16	27-Jan-16	357d			■ Re-provision of permanent jetty and floating pontoon - RHKYC Inspection / Appvl											
Phase 3 Mooring Re-Arrangement																							
S5_55940		Phase 3 Mooring Re-Arrangements in area of TS4/ME4	6d/wk	12d	03-Jun-14	16-Jun-14	29-Jan-14	14-Feb-14	-97d			■ Phase 3 Mooring Re-Arrangements in area of TS4/ME4											
TS4 - OHVD / Cable Trough																							
S5_6185		TS4 (incl. TS4+) - OHVD Slab - Area C (access through temp. opening at TZ4)	6d/wk	60d	02-Jan-15*	16-Mar-15	10-Jun-15	20-Aug-15	127d			■ TS4 (incl. TS4+) - OHVD Slab - Area C (access through temp. opening at TZ4)											
S5_6190		TS4 (incl. TS4+) - Cable Trough (access through temp. opening at TZ4)	6d/wk	60d	17-Mar-15	01-Jun-15	21-Aug-15	02-Nov-15	127d			■ TS4 (incl. TS4+) - Cable Trough (access through temp. opening at TZ4)											
S5_59850		Completion of Section 5 - TS4/ME4 Area (KD10), below -20mPD	7d/wk-2	0d		02-Nov-15*		02-Nov-15	0d			◆ Completion of Section 5 - TS4/ME4 Area (KD10), below -20mPD											
Works in TPCWAE Area (Portion 20A, 20B)																							
MT West Portal Works																							
WB (West Bound) Tunnel																							
S67820		WB Tunnel Base Slab - 5m Base slab + kicker wall	7d/wk-1	6d	15-Oct-13 A	24-Oct-13	19-Jun-13	25-Jun-13	-117d	■	WB Tunnel Base Slab - 5m Base slab + kicker wall												
S67800		WB Assemble arc lining shutter (outside)	7d/wk-1	6d	25-Oct-13	30-Oct-13	26-Jun-13	02-Jul-13	-117d	■	WB Assemble arc lining shutter (outside)												
S67810		WB Tunnel Arc Concrete lining - 5m	7d/wk-1	18d	31-Oct-13	17-Nov-13	03-Jul-13	20-Jul-13	-117d	■	WB Tunnel Arc Concrete lining - 5m												
EB (East Bound) Tunnel																							
S67785		EB Mined Tunnel "Inner" Excavation - 7m (Arch rib->Mining->Shotcrete)	7d/wk-1	27d	02-Sep-13 A	19-Oct-13	18-Jun-13	19-Jun-13	-118d	■	EB Mined Tunnel "Inner" Excavation - 7m (Arch rib->Mining->Shotcrete)												
S67815		EB Tunnel Base Slab - 5m Base slab + kicker wall	7d/wk-1	6d	20-Oct-13	25-Oct-13	20-Jun-13	25-Jun-13	-118d	■	EB Tunnel Base Slab - 5m Base slab + kicker wall												
S67795		EB Assemble arc lining shutter (outside)	7d/wk-1	6d	26-Oct-13	31-Oct-13	26-Jun-13	02-Jul-13	-118d	■	EB Assemble arc lining shutter (outside)												
S67805		EB Tunnel Arc Concrete lining - 5m	7d/wk-1	18d	01-Nov-13	18-Nov-13	03-Jul-13	20-Jul-13	-118d	■	EB Tunnel Arc Concrete lining - 5m												
CCT RC Structure																							
■ Remaining Work																							
◆ Remaining Work																							
■ Critical Remaining Work																							
◆ Milestone																							
■ Summary																							
■ Summay																							
5 of 13																							
Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)																							
WORKS PROGRAMME REV. J																							
