Civil Engineering and Development Department

Trunk Road T2 Monthly Environmental Monitoring and Audit Report (under EP-451/2013)

June 2022 (Version 1.0)

Approved By

(Environmental Team Leader:

Mr. KS Lee)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

CINOTECH CONSULTANTS LTD

Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong Tel: (852) 2151 2083 Fax: (852) 3107 1388 Email: info@cinotech.com.hk



Ref.: CEDKTDT2EM00_0_0362L.22

13 July 2022

By Post and Email

Hyder-Meinhardt Joint Venture 17/F, Two Harbour Square 180 Wai Yip Street, Kwun Tong Kowloon, Hong Kong

Attention: Mr. Edwin China

Dear Mr. Ching,

Re: Agreement No. EDO 01/2019
Independent Environmental Checker for
Contract No. ED/2018/04 – Trunk Road T2 and Infrastructure Works for
Developments at the Former South Apron

Monthly EM&A Report (June 2022) for EP-451/2013

Reference is made to the Environmental Team's submission of the Monthly EM&A Report for June 2022 (Version 1.0) certified by the ET Leader and provided to us via e-mail on 13 July 2022. We are pleased to inform you that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 of EP-451/2013.

The ET Leader is reminded that it is the ET's responsibility to ensure the report be timely submitted to the Director of Environmental Protection as per Condition 3.4 of EP-451/2013.

Thank you for your attention. Please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely, For and on behalf of Ramboll Hong Kong Limited

Y H Hui

Independent Environmental Checker

c.c.

CEDD

Attn.: Mr. Tommy Wong

Fax: 2739 0076

BTP

Attn.: Mr. Ivan Chau

By email

Cinotech

Attn.: Mr. K. S. Lee

Fax: 3107 1388

Q:\Projects\CEDKTDT2EM00\02 Proj_Mgt\02 Corr\CEDKTDT2EM00_0_0362L.22.doc

TABLE OF CONTENTS

		1 age
EX	KECUTIVE SUMMARY	1
	Introduction	1
	Summary of Main Works Undertaken and Key Measures Implemented	
	Summary of Exceedances, Investigation and Follow-up	
	Complaint Handling, Prosecution and Public Engagement	2
	Reporting Changes	
	Future Key Issues	
	Review of Status and Location of Monitoring Stations	4
1	INTRODUCTION	5
	Background	5
	Purpose of the Report	
	Project Organizations	6
	Construction Activities undertaken during the Reporting Month	
	Summary of EM&A Requirements	
	Status of Environmental Licensing and Permitting	8
2	AIR QUALITY	9
	Monitoring Requirement	9
	Monitoring Locations	9
	Monitoring Parameters and Frequency	
	Monitoring Equipment	
	Monitoring Methodology	10
	Results and Observations	13
	Comparison of EM&A Result with EIA Prediction	14
3	NOISE	15
	Monitoring Requirements	15
	Monitoring Locations.	
	Monitoring Parameters, Frequency and Duration	
	Monitoring Equipment	16
	Monitoring Methodology and QA/QC Procedure	16
	Maintenance and Calibration	
	Results and Observations	
	Comparison of EM&A Result with EIA Prediction	
4	WATER QUALITY	19
	Monitoring Requirement	19
5	MARINE ECOLOGY	19
6	FISHERIES	19
7	LANDSCAPE AND VISUAL	20
8	CULTURAL HERITAGE	23
9	WASTE MANAGEMENT	23

10 EN	IVIRONMENTAL AUDIT24	
Si	te Audits24	
	pplementation Status of Environmental Mitigation Measures	
	rplementation Status of Event and Action Plans25	
	atus of Required Submission under Environmental Permit	
11 ENVIRONMENTAL NON-CONFORMANCE		
	ummary of Complaint, Warning, Notification of any Summons and Successful Prosecution27 ummary of Exceedance	
12 FU	TURE KEY ISSUES27	
M	onitoring Schedule	
13 CC	ONCLUSIONS AND RECOMMENDATIONS29	
Co	onclusions	
	ecommendations	
LIST O	OF TABLES	
Table I	Summary of Complaint/Summons/Prosecution in the Reporting Month	
Table II	Summary Table for Site Activities in the next Reporting Period	
Table II		
Table 1.	7	
Table 1.	J	
Table 2.		
Table 2.	5 T 1 (1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	
Table 2.		
Table 3.	6	
Table 3.	1 ,	
Table 3. Table 3.	C 1 1	
Table 3.	y c	
Table 3.		
Table 3.		
Table 7.		
Table 7.	± · · · · · · · · · · · · · · · · · · ·	
Table 10		
Table 10		
14010 1	o.2 Sacas of required Submission under Environmental Fernite	
LIST O	OF FIGURES	

Figure 1.1	Layout Plan of the Project Site
Figure 1.2	Project Organisation for Environmental Monitoring and Audit
Figure 2	Locations of Air Quality and Construction Noise Monitoring Stations

LIST OF APPENDICES

Appendix A	Action and Limit Levels
Appendix B	Environmental Monitoring Schedules
Appendix C	Copies of Calibration Certificates for Air Quality Monitoring
Appendix D	Weather Information
Appendix E	1-hour TSP Monitoring Results and Graphical Presentations (not used)
Appendix F	24-hour TSP Monitoring Results and Graphical Presentations
Appendix G	Copies of Calibration Certificates for Noise Monitoring
Appendix H	Noise Monitoring Results and Graphical Presentations
Appendix I	Site Audit Summary
Appendix J	Event and Action Plans
Appendix K	Environmental Mitigation Implementation Schedule (EMIS)
Appendix L	Summaries of Environmental Complaint, Warning, Summon and Notification of
	Successful Prosecution
Appendix M	Summary of Exceedance
Appendix N	Tentative Construction Programme
Annendix O	Waste Generated in the Reporting Month

EXECUTIVE SUMMARY

Introduction

1. This is the 28th Environmental Monitoring and Audit (EM&A) Report prepared by the Environmental Team (ET), Cinotech Consultants Ltd., for "Trunk Road T2". This report summarized the monitoring results and audits findings of the EM&A programme under the issued Environmental Permit (EP) No. EP-451/2013 and in accordance with the EM&A Manual (AEIAR-174/2013) during the reporting month of June 2022.

Summary of Main Works Undertaken and Key Measures Implemented

2. The main works undertaken during the reporting period are as follows:

Kai Tak:

- Depressed Road Portal Structure, Capping Beam
- Depressed Road DPR/SUS connection
- West Ventilation Building Base slab, Rebar fixing
- Cut & Cover Notch construction
- Westbound TBM Tunnelling
- Eastbound TBM Tunnelling
- EB Service Gallery installation
- ISIG 2 pre-assembly
- CKL Junction Reinstatement works
- Road S20 / AMAWBC Road & Drain
- Road L10 (North) ELS part 2
- Road L10 (North) RC Structure
- Road L18 Sheet Pile
- Outfall 1 Construction
- District Cooling System (DCS) Section 6B Testing & Commissioning
- District Cooling System (DCS) Section 7B
- District Cooling System (DCS) Pipe Jacking ELS
- Foot Bridge (FB-02) H Pile Installation
- Foot Bridge (FB-02) Temporary Ramp Construction
- Foot Bridge (FB-02) Pile Cap Construction
- Foot Bridge (FB-02) Pier Construction
- 3. Implementation of the key mitigation measures during the reporting period are as follows:

Air Quality

- Water spraying regularly on construction site area to avoid dust generation.
- Excavated dusty materials were covered by impervious sheets.

Noise

- Air compressor was operated with door closed and have valid noise labels.
- Use of Quality Powered Mechanical Equipment (QPME)
- Erecting noise barriers on site to minimize noise impact generated from breaking activities.

Water Quality

• WetSep was constructed to treat the surface runoff prior to discharge.

Landscape and Visual

• Tree protection zone were fenced off to protect the existing tree.

Summary of Exceedances, Investigation and Follow-up

4. Exceedance of Action/Limit levels during the reporting month (June 2022) and the investigation results and/or follow-up actions:

Air Quality Monitoring

- No Action Level exceedance for 24-hour TSP was recorded.
- No Limit Level exceedance for 24-hour TSP was recorded.

Construction Noise Monitoring

- No Limit Level exceedance for day time construction noise was recorded in this reporting month.
- No Action Level exceedance was recorded in this reporting month.

Landscape and Visual Monitoring and Audit

• No non-compliance of the landscape and visual impact was recorded in the reporting month. The implementation of landscape and visual and mitigation measures was checked by a Registered Landscape Architect (RLA) during the environmental site inspections.

Complaint Handling, Prosecution and Public Engagement

Table I Summary of Complaint/Summons/Prosecution in the Reporting Month

Event	Event Details		Follow-up/	Status/
Event	Number	Brief Description	Remedial Actions	Remarks
Complaints Received	0	-	-	-
Notification of Summons and Prosecutions Received	0	-	-	-
Public Engagement Activities	0	-	-	-

Reporting Changes

5. No reporting change in this reporting month.

Future Key Issues

6. The key works or activities will be anticipated in the next reporting period are as follows:

Table II Summary Table for Site Activities in the next Reporting Period

Site Activities (July 2022)	Key Environmental Issues
 Depressed Road – Portal Structure, Capping Beam Depressed Road – DPR/SUS connection Cut & Cover Notch construction Westbound TBM Tunnelling Eastbound TBM Tunnelling EB Service Gallery installation ISIG 2 pre-assembly CKL Junction Reinstatement works Road S20 / AMAWBC – Road & Drain Road L10 (North) ELS part 2 Road L10 (North) RC Structure Road L18 – Sheet Pile Outfall 1 Construction District Cooling System (DCS) Section 6B Testing & Commissioning District Cooling System (DCS) Pipe Jacking ELS District Cooling System (DCS) Pipe Jacking ELS District Cooling System (DCS) Pipe Jacking Foot Bridge (FB-02) H Pile Installation Foot Bridge (FB-02) Pier Construction Foot Bridge (FB-02) Bridge Deck Construction CP Tympanum construction 	(A) / (B) / (C) / (D)

Note:

- (C) Runoff from exposed slope or site area; and
- (D) Wastewater and runoff discharge from site.

⁽A) Dust generation from haul road, stockpile of dusty materials, exposed site area, excavation works and rock breaking activities;

⁽B) Noisy construction activity such as rock-breaking activities and piling works;

Review of Status and Location of Monitoring Stations

7. According to the EM&A Manual (AEIAR-174/2013), the number and location of the monitoring stations and parameters should be reviewed in every six months, or on as -needed basis, in order to cater for any changes in the surrounding environmental and the nature of works in progress. The latest review was conducted in February 2022 and the review of status and location of monitoring stations are summarized as follow:

Table III Summary Table for Review of Status and Location of Monitoring Stations

Monitoring Station ID	Review Status	Follow-up Action/ Recommendation
KTD 2d	ET has reviewed the status and location	
KER1	of KER1, KTD 1, KTD2d, CKL1 and CKL2. To conclude, the environmental	
KTD 1	monitoring conducted at KER1, KTD 1, KTD2d, CKL 1 and CKL 2 are appropriate, and the monitoring results	N/A
CKL 1	reflect how the sensitive receiver(s) is/are impacted by the construction	
CKL 2	activities of the Project.	

N/A: Not Applicable

1 INTRODUCTION

Background

- 1.1 In 2009, Civil Engineering and Development Department (CEDD) commissioned a Kai Tak Development (KTD) Trunk Road T2 and Infrastructure at South Apron Investigation. The assignment covers the provision of the Trunk Road T2 and its connections with the Central Kowloon Route (CKR) at the north apron area and the Tseung Kwan O Lam Tin Tunnel (TKOLTT) to the south in the Cha Kwo Ling area.
- 1.2 The Trunk Road T2 Project is one of the designated Projects under Schedule 2 of the EIAO proposed in the KTD. CEDD submitted the Project Profile (No. PP-379/2009) on 24 March 2009 for application for an EIA study brief for the Trunk Road T2 Project under the EIAO. Accordingly, an EIA Study Brief (ESB-203/2009) for the Trunk Road T2 Project was issued on 30 April 2009. The Environmental Impact Assessment (EIA) Report for the Trunk Road T2 Project was approved under the Environmental Impact Assessment Ordinance (EIAO) on 19 September 2013. The corresponding Environmental Permit (EP) was issued on 19 September 2013 (EP no.: EP-451/2013).
- 1.3 The Contract No. ED/2018/04 is the main contract of Trunk Road T2 ("T2 Main Works") which comprises mainly the design and construction of a dual two-lane trunk road of approximately 3.0km long with about 2.7km of the trunk road in form of tunnel; ventilation and administration buildings, environmental protection and mitigation works and etc. The EM&A programme at Kai Tak area under this Contract is governed by the EP-451/2013 and EM&A Manual (AEIAR-174/2013). The work areas of the T2 Main Works are shown in **Figure 1** and the works to be executed under this Contract and corresponding EP is summarized as follows:

Environmental Permit	Works Description
EP-451/2013 – Trunk Road T2	<u>Trunk Road T2</u>
	Construction of highway and sub-sea tunnel connecting between
	Central Kowloon Route and Cha Kwo Ling Tunnel
	Western & Eastern Ventilation Buildings

Monitoring Works in Kai Tak under EP-451/2013

1.4 Under Contract No. KL/2014/03 - Kai Tak Development - Stage 3 Infrastructure Works for Development at the Southern Part of the Former Runway ("T2 Advance Works"), the baseline monitoring works in Kai Tak under the EM&A Manual (AEIAR-174/2013) were conducted by the Environmental Team (ET) for the Contract No. KL/2014/03 at the approved relocated monitoring locations (EPD reference: EP2/K19/A/21 pt.5), namely KTD1a, KTD2a & KER1a. During the impact monitoring period, monitoring locations KTD 2a and KER 1a were relocated to new locations, i.e. KTD 2b and KER 1b (EPD reference: () in EP2/K19/A/21 pt. 6 and () in EP2/K19/A/21 pt. 5) respectively. Location KTD2b was then further relocated to location KTD2c, the proposal of such relocation was submitted to EPD on 24 March 2020 and was approved by EPD on 6 April 2020 (EPD reference: () in EP2/K19/A/21 pt.7). The aforementioned relocation was effective from 9 April 2020. Since the major part of work under Contract No. KL/2014/03 has been completed and monitoring works conducted by the ET of Contract No. KL/2014/03 was determined to be ceased, the impact monitoring within the Kai Tak area was then handed over to the ET of Contract No. ED/2018/04 on 1 August 2020. The monitoring location has been reviewed and updated to obtain the data with higher representative

based on several conditions, such as distance between monitoring location and the sensitive receiver, non-project related interference, obstruction to the construction works on site and the power supply problem. The monitoring location KTD1a and KER1b has been updated to the monitoring location KTD1 and KER1 on 3 August 2020, where are the original location as proposed in the EM&A manual (AEIAR-174/2013). And the monitoring location KTD2c was remained unchanged after the aforementioned review. Location KTD2c was then further relocated to location KTD2d, the proposal of such relocation was submitted on 9 March 2021 and was approved by EPD on 3 27th 2021 (EPD reference: () in EP2/K19/A/21 pt.8). The aforementioned relocation was effective from 24 May 2021. The impact monitoring for the three stations KTD1, KTD2d and KER1 are currently conducted by the ET of T2 Main Works

Monitoring Works in Cha Kwo Ling under EP-451/2013

- 1.5 The environmental impact of the remaining works in Cha Kwo Ling, under EP-451/2013, shall be monitored at the two proposed stations, namely CKL1, CKL2, in accordance to the EM&A Manual (AEIAR-174/2013). The impact monitoring for the two proposed stations shall be conducted by the ET of T2 Main Works.
- 1.6 Cinotech Consultants Ltd. was designated as the Environmental Team (ET) to undertake the EM&A works for "Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron" (hereinafter called the "Project").

Purpose of the Report

1.7 This is the 28th Monthly EM&A Report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period in June 2022

Project Organizations

- 1.8 Different Parties with different levels of involvement in the Project organization include:
 - Permit Holder Civil Engineering and Development Department (CEDD)
 - Supervisor Representative Hyder-Meinhardt Joint Venture (HMJV)
 - Environmental Team (ET) Cinotech Consultants Limited (Cinotech)
 - Independent Environmental Checker (IEC) Ramboll Hong Kong Limited (Ramboll)
 - Contractor Bouygues Travaux Publics (BTP)
- 1.9 The key contacts of the Project are shown in **Table 1.1**.

Table 1.1 Key Project Contacts

Party	Role	Contact Person	Phone No.
CEDD	Permit Holder	Mr. Wong Chi Wai, Tommy	3842 7111
HMJV	Supervisor Representative	Ms. Hazel Tang	2149 8524
Cin atash Environmental Taom		Mr. KS Lee (ETL)	2151 2091
Cinotech	Environmental Team	Ms. Karina Chan	2157 3880

Party	Role	Contact Person	Phone No.
Ramboll	Independent Environmental Checker	Mr. YH Hui	3465 2850
ВТР	Contractor	Ms. Ality Chan	5185 4462

1.10 The Organizational Structure for Environmental Management is shown in **Figure 1.2**.

Construction Activities undertaken during the Reporting Month

1.11 The major site activities undertaken in the reporting month included:

Kai Tak:

- Depressed Road Portal Structure, Capping Beam
- Depressed Road DPR/SUS connection
- West Ventilation Building Base slab, Rebar fixing
- Cut & Cover Notch construction
- Westbound TBM Tunnelling
- Eastbound TBM Tunnelling
- EB Service Gallery installation
- ISIG 2 pre-assembly
- CKL Junction Reinstatement works
- Road S20 / AMAWBC Road & Drain
- Road L10 (North) ELS part 2
- Road L10 (North) RC Structure
- Road L18 Sheet Pile
- Outfall 1 Construction
- District Cooling System (DCS) Section 6B Testing & Commissioning
- District Cooling System (DCS) Section 7B
- District Cooling System (DCS) Pipe Jacking ELS
- Foot Bridge (FB-02) H Pile Installation
- Foot Bridge (FB-02) Temporary Ramp Construction
- Foot Bridge (FB-02) Pile Cap Construction
- Foot Bridge (FB-02) Pier Construction
- 1.12 The EM&A programme requires construction noise, air quality monitoring and environmental site audit, etc. The EM&A requirements for each parameter are described in the following sections, including:
 - All monitoring parameters;
 - Action and Limit levels for all environmental parameters;
 - Event Action Plans;
 - Environmental mitigation measures, as recommended in the Project EIA Report.
- 1.13 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in **Section 10** of this report.
- 1.14 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the monitoring parameters of the required environmental monitoring works and audit works for the Project in June 2022.

Status of Environmental Licensing and Permitting

1.15 All permits/licenses obtained for the Project are summarized in **Table 1.3**.

Table 1.3 Summary of Environmental License and Permit

D	Valid Period		G
Permit / License No.	From	То	Status
Environmental Permit (EP)			
EP-451/2013	19 Sep 2013	N/A	Valid
Notification pursuant to Air Pollution (Cons	truction Dust) F	Regulation	
Ref. No.: 451120	20 Nov 2019	N/A	Valid
Billing Account for Construction Waste Disp	osal		
A/C No.: 7036016	09 Dec 2019	N/A	Valid
Billing Account for Vessel Disposal	•		
A/C No.:7037747 (Application No.: CEDD01146)	13 Apr 2022	25 Jul 2022	Valid
Construction Noise Permit			
CNP No.(For Junction of Hoi Bun Road and Kai Hing Road): GW-RE1272-21	30 Dec 2021	22 Jun 2022	Expired on 22 Jun 2022
CNP No. (For Depressed Road and Support Area): GW-RE0220-22	26 Mar 2022	25 Sep 2022	Valid
CNP No. (For Launching Shaft and Barging Point): GW-RE0123-22	25 Feb 2022	24 Aug 2022	Valid
Wastewater Discharge License	•		
WT00036183-2020 (For Depressed Road Area)	27 Jul 2020	31 Jul 2025	Valid
WT00036228-2020 (For Launching Shaft)	10 Nov 2021	31 Jul 2025	Valid
WT00039117-2021 (For Site Office and Support Area)	28 Sep 2021	30 Sep 2026	Valid
Chemical Waste Producer License			
WPN: 5213-286-B2557-03	09 Mar 2020	N/A	Valid

2 AIR QUALITY

Monitoring Requirement

2.1 According to the EM&A Manual (AEIAR-174/2013), 24-hour Total Suspended Particulates (TSP) monitoring was conducted to monitor the air quality for this Project. For regular impact monitoring, a sampling frequency of at least once in every six days at all of the monitoring stations for 24-hour TSP monitoring. In case of complaints, 1-hour TSP monitoring should be conducted at least three times in every six days when the highest dust impacts are likely to occur. Appendix A shows the established Action/Limit Levels for the environmental monitoring works.

Monitoring Locations

- 2.2 Five designated monitoring stations were selected for air quality monitoring programme. **Table 2.1** describes the air quality monitoring locations, which are also depicted in **Figure 2**.
- 2.3 The monitoring location at Kai Tak area has been reviewed and updated to obtain the data with higher representative based on several conditions, such as distance between monitoring location and the sensitive receiver, non-project related interference, obstruction to the construction works on site and the power supply problem. The monitoring location KTD1a and KER1b has been updated to KTD1 and KER1 respectively, where are the original location as proposed in the EM&A manual (AEIAR-174/2013). And the monitoring location KTD2c was remained unchanged after the aforementioned review. Monitoring location KTD2c was then further relocated to KTD2d after the review of status and location of monitoring station conducted in between February and March 2021.

Table 2.1 Air Quality Monitoring Locations

Monitoring Stations	Location
KTD1	Centre of Excellence in Paediatrics (Children's Hospital)
KTD2d	Next to the SOR Office of Trunk Road T2 in Kai Tak Area
KER1	Future Residential Development at Kerry Godown
CKL1	Flat 121 Cha Kwo Ling Village
CKL2	Flat 103 Cha Kwo Ling Village

Monitoring Parameters and Frequency

2.4 **Table 2.2** summarizes the monitoring parameters, monitoring period and frequencies of impact air quality monitoring. The monitoring schedule is shown in **Appendix B**.

Table 2.2 Frequency and Parameters of Air Quality Monitoring

Monitoring Stations	Parameter	Period	Frequency
KTD1, KTD2d, KER1, CKL1 & CKL2	1-hour TSP	0700 – 1900	3 times per 6 days (as required in case of complaints)
KTD1, KTD2d, KER1, CKL1 & CKL2	24-hour TSP	24 hours	Once every 6 days

Monitoring Equipment

- 2.5 High Volume Samplers (HVS) in compliance with the specification stipulated in the EM&A Manual (AEIAR-174/2013), Section 2.2.1.4, were used to carry out 24-hour TSP monitoring. Direct reading dust meter were also used to measure 1-hour average TSP levels. The 1-hour sampling was determined by HVS to check the validity and accuracy of the results measured by direct reading method.
- 2.6 Wind data monitoring equipment was set at rooftop (about 41/F) of Yau Lai Estate Bik Lai House, Lam Tin for logging wind speed and wind direction such that the wind sensors were clear of obstructions or turbulence caused by building. The wind data monitoring equipment was recalibrated at least once every six months and the wind directions were divided into 16 sectors of 22.5 degrees each. Wind data is attached in **Appendix D**.
- 2.7 **Table 2.3** summarizes the equipment used for air quality monitoring. Copies of calibration certificates are attached in **Appendix C**.

Table 2.3 Air Quality Monitoring Equipment

Equipment	Model	Quantity
HVS Sampler	TISCH Model: TE-5170 (Serial no. 0723, 1956, 10595, 1316, 5280)	5
Calibrator	TISCH Model: TE-5025A (Serial no. 3864)	1
Wind Anemometer	Davis Weather Monitor II, Model no. 7440 (Serial no. MC01010A44)	1

Monitoring Methodology

1-hour TSP Monitoring

Measuring Procedures

2.8 The measuring procedures of the 1-hour dust meter are in accordance with the Manufacturer's Instruction Manual as follows:

(Sibata Model No.: LD-3B/LD-5R)

- The 1-hour dust meter is placed at least 1.3 meters above ground.
- Set POWER to "ON" and make sure that the battery level was not flash or in low level.
- Allow the instrument to stand for about 3 minutes and then the cap of the air sampling inlet has been released.
- Push the knob at MEASURE position.

- Set time/mode setting to [BG] by pushing the time setting switch. Then, start the background measurement by pushing the start/stop switch once. It will take 6 sec. to complete the background measurement.
- Push the time setting switch to change the time setting display to [MANUAL] at the bottom left of the liquid crystal display. Finally, push the start/stop switch to stop the measuring after 1 hour sampling.
- Information such as sampling date, time, count value and site condition were recorded during the monitoring period.

Maintenance/Calibration

- 2.9 The following maintenance/calibration is required for the 1-hour dust meter:
 - Check and calibrate the meter by HVS to check the validity and accuracy of the results measured by direct reading method at 2-month intervals throughout all stages of the air quality monitoring.

24-hour TSP Monitoring

Instrumentation

- 2.10 High volume samplers (HVS) (TISCH Model: TE-5170) complete with appropriate sampling inlets was employed for 24-hour TSP monitoring. The sampler was composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complied with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50). Moreover, the HVS also met all the requirements in Section 2.2 of the Annex II Specification.
- 2.11 The positioning of the HVS samplers are as follows:
 - A horizontal platform with appropriate support to secure the samplers against gusty wind shall be provided;
 - No two samplers shall be placed less than 2 meter apart;
 - The distance between the sampler and an obstacle, such as buildings, must be at least twice the height that the obstacle protrudes above the sampler;
 - A minimum of 2 metres of separation from walls, parapets and penthouses is required for rooftop samplers;
 - A minimum of 2 metres of separation from any supporting structure, measured horizontally is required;
 - No furnace or incinerator flue is nearby;
 - Airflow around the sampler is unrestricted;
 - The sampler is more than 20 metres from the dripline;
 - Any wire fence and gate, to protect the sampler, shall not cause any obstruction during monitoring;
 - Permission must be obtained to set up the samplers and to obtain access to the monitoring stations; and
 - A secured supply of electricity is needed to operate the samplers.

Operating/analytical procedures for the operation of HVS

- 2.12 Operating/analytical procedures for the air quality monitoring are highlighted as follows:
 - Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 0.6 m³/min. and 1.7 m³/min.) in accordance with the EM&A manual (AEIAR-174/2013). The flow rate shall be indicated on the flow rate chart.
 - For TSP sampling, fiberglass filters with a collection efficiency of > 99% for particles of 0.3 µm diameter were used.
 - The power supply was checked to ensure the sampler worked properly. On sampling, the sampler was operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air monitoring station.
 - The filter holding frame was then removed by loosening the four nuts and a weighted and conditioned filter was carefully centered with the stamped number upwards, on a supporting screen.
 - The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
 - The shelter lid was closed and secured with the aluminum strip.
 - The timer was then programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).
 - After sampling, the filter was removed and sent to the HOKLAS laboratory (High Precision Chemical Testing Ltd.) for weighing. The elapsed time was also recorded.
 - Before weighing, all filters were equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than ±3°C; the relative humidity (RH) should be < 50% and not vary by more than ±5%. A convenient working RH is 40%.

Maintenance/Calibration

- 2.13 The following maintenance/calibration is required for the HVS:
 - The high volume motors and their accessories were properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking were made to ensure that the equipment and necessary power supply are in good working condition.
 - High volume samplers were calibrated at bi-monthly intervals using TE-5025A Calibration Kit throughout all stages of the air quality monitoring.

Results and Observations

- 2.14 Impact air quality monitoring was conducted at five monitoring stations as scheduled. The monitoring schedule is shown in **Appendix B**.
- 2.15 No Action and Limit Level exceedance was recorded for 24-hour TSP monitoring in the reporting month. Details of the exceedance are presented in **Appendix M**.
- 2.16 The air temperature, relative humidity, and the precipitation data were obtained from daily extracts of Hong Kong Observatory Climate Information Service. This weather information for the reporting month is summarized in **Appendix D**.
- 2.17 The monitoring data and graphical presentations of 24-hour TSP monitoring results are shown in **Appendix F**.
- 2.18 According to field observations observed in the reporting period, the major dust source identified at the designated air quality monitoring stations are as follows:

Table 2.4 Major Dust Source during Air Quality Monitoring

Monitoring Stations	Major Dust Source
KTD 1 - Centre of Excellence in Paediatrics (Children's Hospital)	 Project related construction activities (i.e., Loading and unloading of C&D wastes, drilling, crushing of material); Vehicle movement in the site;
KER 1 – Future Residential Development at Kerry Godown	 Construction activities at the nearby construction sites of New Acute Hospital; and, Road traffic along Shing Fung Road, Shing Cheong Road, Cheung Yip Street, Kai Hing Road and Kwun Tong Bypass.
KTD 2d – Next to the SOR Office of Trunk Road T2 in Kai Tak Area	 Project related construction activities (i.e., Loading and unloading of C&D material, crushing of material); Vehicle movement in the site; and, Non-project related construction activities
CKL1 - Flat 121 Cha Kwo Ling Village	Road Traffic along Cha Kwo Ling Road
CKL2 - Flat 103 Cha Kwo Ling Village	Road Traffic along Cha Kwo Ling Road

Comparison of EM&A Result with EIA Prediction

2.19 The air monitoring data was compared with the predictions in Table 4.14 of EIA Report, AEIAR-174/2013 (as approved in 2013) as summarised in **Table 2.6** for 24-hour TSP.

Table 2.6 Comparison of 24-hr TSP Monitoring Data with Predictions in EIA Report

Monitoring Stations	ASR ID	Predicted Maximum 24-hr TSP Concentration in EIA Report (AEIAR- 174/2013), μg/m ³	Maximum 24-hr TSP Concentration in the Reporting Month (June 2022), μg/m ³
KTD 1 - Centre of Excellence in Paediatrics (Children's Hospital)	KTD3	126	39.2
KTD 2d – Next to the SOR Office of Trunk Road T2 in Kai Tak Area	N/A ⁽¹⁾	N/A ⁽¹⁾	76.9
KER 1 – Future Residential Development at Kerry Godown	KTD6	169	136.5
CKL1 - Flat 121 Cha Kwo Ling Village	N/A ⁽¹⁾	N/A ⁽¹⁾	85.6
CKL2 - Flat 103 Cha Kwo Ling Village	N/A ⁽¹⁾	N/A ⁽¹⁾	88.2

Remarks:

2.20 In the reporting month the 24-hour TSP concentration at KTD1 and KER1 were lower than the prediction in the EIA Report, AEIAR-174/2013 (as approved in 2013). No Action and Limit level exceedance for 24-hour TSP was recorded in the reporting period.

⁽¹⁾ No 24-hr TSP concentration was predicted in EIA Report (AEIAR-174/2013)

3 NOISE

Monitoring Requirements

3.1 According to the EM&A Manual (AEIAR-174/2013), construction noise monitoring was conducted to monitor the construction noise arising from the construction activities. The regular monitoring frequency for each monitoring station shall be on a weekly basis and conduct one set of measurements between 0700 and 1900 hours on normal weekdays. **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.

Monitoring Locations

- 3.2 Noise monitoring was conducted at five designated monitoring stations, namely KTD1, KTD2d, KER1, CKL1 and CKL2 in the reporting period. **Table 3.1** and **Figure 2** show the locations of these stations.
- 3.3 The monitoring location at Kai Tak area has been reviewed and updated to obtain the data with higher representative based on several conditions, such as distance between monitoring location and the sensitive receiver, non-project related interference, obstruction to the construction works on site and the power supply problem. The monitoring location KTD1a and KER1b has been updated to KTD1 and KER1 respectively, where are the original location as proposed in the EM&A manual (AEIAR-174/2013). And the monitoring location KTD2c was remained unchanged after the aforementioned review. Monitoring location KTD2c was then further relocated to KTD2d after the review of status and location of monitoring station conducted in between February and March 2021.

Table 3.1 Noise Monitoring Stations

Monitoring Stations	Location
KTD1	Centre of Excellence in Paediatrics (Children's Hospital)
KTD2d Next to the SOR Office of Trunk Road T2 in Kai Tak Area	
KER1	Future Residential Development at Kerry Godown
CKL1	Flat 121 Cha Kwo Ling Village
CKL2	Flat 103 Cha Kwo Ling Village

Monitoring Parameters, Frequency and Duration

3.4 **Table 3.2** summarizes the monitoring parameters, frequency and total duration of monitoring. The noise monitoring schedule is shown in **Appendix B**.

Monitoring Stations	Time Period	Duration	Frequency	Parameter	Measurement
KTD1					Façade Measurement
				$L_{10}(30 \text{ min.})$	Eng End Management
KTD2d				dB(A)	Free Field Measurement
	0700-1900 hrs		Once per	L ₉₀ (30 min.)	Free Field Measurement
KER1	on normal	30 minutes	week	dB(A)	Tree Freid Wiedsdreinent
CVI 1	weekdays			T (20 :)	Free Field Measurement
CKL1				$L_{eq}(30 \text{ min.})$	
CKL2				dB(A)	Free Field Measurement

Table 3.2 Frequency and Parameters of Noise Monitoring

Monitoring Equipment

3.5 Integrating Sound Level Meter was used for impact noise monitoring. The meters were Type 1 sound level meter capable of giving a continuous readout of the noise level readings including equivalent continuous sound pressure level (L_{eq}) and percentile sound pressure level (L_x) that also complied with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications. **Table 3.3** summarizes the noise monitoring equipment being used within the reporting period. Copies of calibration certificates are attached in **Appendix G**.

Table 3.3 Noise Monitoring Equipment

Equipment	Model	Quantity
Integrating Sound Level Meter	BSWA 308 (Serial no. 580287)	1
	SVAN 957 (Serial no. 23852, 23851)	2
Calibrator	ST-120 (Serial no. 181001608)	1
Cambrator	SV 30A (Serial no. 10965)	1

Monitoring Methodology and QA/QC Procedure

- 3.6 The monitoring procedures are as follows:
 - The monitoring station was normally be at a point 1m from the exterior of the sensitive receivers building façade and be at a position 1.2m above the ground.
 - For free field measurement, the meter was positioned away from any nearby reflective surfaces. All records for free field noise levels were adjusted with a correction of +3 dB(A).
 - The battery condition was checked to ensure the correct functioning of the meter.
 - Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - Frequency weighting: A
 - Time weighting: Fast
 - Time measurement: 30 minutes
 - Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement was more than 1.0 dB, the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.

- The wind speed was frequently checked with the portable wind meter.
- At the end of the monitoring period, the L_{eq}, L₉₀ and L₁₀ were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- Noise monitoring would be cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s. Supplementary monitoring would be provided to ensure sufficient data would be obtained.

Maintenance and Calibration

- 3.7 The microphone head of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.
- 3.8 The sound level meter and calibrator were checked and calibrated at yearly intervals.
- 3.9 Immediately prior to and following each noise measurement the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements were accepted as valid only if the calibration levels from before and after the noise measurement agree to within 1.0 dB.

Results and Observations

- 3.10 Impact noise monitoring was conducted at five monitoring stations as scheduled. The monitoring schedule is shown in **Appendix B**. No Action/ Limit Level exceedance was recorded for day time construction noise monitoring in the reporting month.
- 3.11 Noise monitoring results and graphical presentations are shown in **Appendix H**.
- 3.12 According to field observations observed in the reporting period, the major noise sources identified at the noise monitoring stations are shown in **Table 3.4**.

Table 3.4 Other Noise Source Identified during Noise Monitoring

Monitoring Stations	Major Noise Source		
KTD 1	 Project related construction activities (Loading and unloading of C&D waste, travel of vehicles, use of PME and other plants, and other construction activities); Vehicle movement in the site; Road traffic along Shing Cheong Road; and, Non-project related construction activities at the nearby construction site of New Acute Hospital. 		
KTD 2d	 Project related construction activities (Loading and unloading of C&D waste, travel of vehicles, use of PME and other plants, and other construction activities); Vehicle movement in the site; and, Non-project related construction activities. 		
KER 1	 Road traffic along Kai Hing Road. Project related construction activities (Travel of vehicles, use of PME and other plants, and other construction activities) 		
CKL1	Road traffic along Cha Kwo Ling Road.		
CKL2	Road traffic along Cha Kwo Ling Road		

3.13 The baseline noise level and the Noise Limit Level at each designated noise monitoring station are presented in **Table 3.5**.

Table 3.5 Baseline Noise Level and Noise Limit Level for Monitoring Stations

Monitoring Stations	Baseline Noise Level, dB (A) (at 0700 – 1900 hrs on normal weekdays)	Noise Limit Level, dB (A) (at 0700 – 1900 hrs on normal weekdays)
KTD1	78	
KTD2d	64	
KER1	65	75
CKL1	72.4	
CKL2	71.4	

Comparison of EM&A Result with EIA Prediction

3.14 The noise monitoring data was compared with the predictions in Table 5.13 of EIA Report (AEIAR-174/2013) as summarised in **Table 3.6**.

Table 3.6 Maximum Predicted Mitigated Construction Noise Levels in EIA Report

Monitoring Stations	NSR ID	Maximum Predicted Mitigated Construction Noise Levels in EIA Report (AEIAR- 174/2013), dB(A)	Maximum Construction Noise Levels in the Reporting Month (June 2022), Leq (30min) dB(A)
KTD 1 - Centre of Excellence in Paediatrics (Children's Hospital)	KTD1	74	72.0
KTD2d – Next to the SOR Office of Trunk Road T2 in Kai Tak Area	N/A ⁽¹⁾	N/A ⁽¹⁾	74.3
KER 1 – Future Residential Development at Kerry Godown	KER1	75	72.2
CKL1 - Flat 121 Cha Kwo Ling Village	CKL4	71	73.7
CKL2 - Flat 103 Cha Kwo Ling Village	CKL5	69	72.9

Remarks:

 $(1): No\ Maximum\ Predicted\ Mitigated\ Construction\ Noise\ Levels\ was\ predicted\ in\ EIA\ Report\ (AEIAR-174/2013)$

3.15 The results at CKL1 and CKL2 were higher than the maximum predicted mitigated construction noise level in the EIA Report, AEIAR-174/2013 (as approved in 2013), this may be due to fluctuations of traffic flow along Cha Kwo Ling Road throughout the day. Besides, the result at KTD1 and KER1 were lower than the maximum predicted mitigated construction noise level in the EIA Report. No Action/ Limit Level exceedance were recorded in the reporting period.

4 WATER QUALITY

Monitoring Requirement

- 4.1 According to Section 4.3.1.1 of EM&A Manual (AEIAR-174/2013), no water quality monitoring is required during the construction phase.
- 4.2 According to Section 4.3.1.5 of EM&A Manual (AEIAR-174/2013), compliance site audits are to be undertaken by the Engineer and ET and escorted by the Contractor to ensure that a valid discharge license has been issued by the EPD prior to the discharge of the effluent from the construction activities of the Project site. Monitoring of the quality of the treated effluent from the works areas should be carried out in accordance with the Water Pollution Control Ordinance (WPCO) license. The audit results reflect whether the effluent quality is in compliance with the discharge license requirements, the summaries of site audits are attached in **Appendix I**.
- 4.3 In the event of non-compliance the responsibilities of the relevant parties is detailed in the Event / Action plan attached in **Appendix J**.

5 MARINE ECOLOGY

- 5.1 According to Section 5.3.1.1 of EM&A Manual (AEIAR-174/2013), ET will be required to undertake audit of good site practice for habitat protection as detailed below. The summaries of site audits are attached in **Appendix I**.
 - Avoid damage and disturbance to the remaining and surrounding natural habitat;
 - Ensure placement of equipment is within designated areas within the existing disturbed land;
 - Ensure construction activities are restricted to within the proposed works boundary;
 - Ensure spoil heaps are be covered at all times;
 - Ensure that disturbed areas are reinstated immediately after completion of the works; and
 - Ensure enhancement planting works undertaken.

6 FISHERIES

- 6.1 According to Section 6.3.1.2 of EM&A Manual (AEIAR-174/2013), no specific fisheries monitoring and audit programme is required during the construction phase.
- 6.2 The implementation of the water quality mitigation measures stated in the Water Quality Impact Assessment (Refer to Section 6 of the EIA Report (AEIAR-174/2013)) will be audited as part of the EM&A procedures during the construction period and the details are presented in **Section 4.2** of this Report. The summaries of site audits are attached in **Appendix I**.

7 LANDSCAPE AND VISUAL

7.1 According to the EM&A Manual (AEIAR-174/2013), a series of mitigation measures were recommended to ameliorate the landscape and visual impacts of the Project. The mitigation measures for construction stage are summarized in **Table 7.1** below and provided in **Appendix K**:

Table 7.1 Construction Phase Landscape and Visual Mitigation Measures

ID No.	Landscape and Visual Mitigation Measure	
CM1	All works shall be carefully designed to minimize impacts on existing landscape resources and visually sensitive receivers. Existing trees within works area shall be retained and protected.	
CM2	Existing trees of good quality and condition that are unavoidably affected by the works should be transplanted.	
CM3	Not used.	
CM4	Not used.	
CM5	Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.	
CM6	Construction plant and building material shall be orderly and carefully stored in order to create a neat and tidy visual appearance	
CM7	Erection of decorative screen hoarding should be designed to be compatible with the existing urban context.	
CM8	All lighting in construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residences and GIC user. The contractor shall consider other security measures, which shall minimize the visual impacts.	

- 7.2 A specialist Landscape Sub-Contractor should be employed by the Contractor for the implementation of landscape construction works and subsequent maintenance operations during the establishment period. It is proposed that the planting works will be on-site and the planting should be completed during the construction contract. The monitoring of the planting establishment should be undertaken for a 12 month period which could extend throughout the Contractor's one-year maintenance period, which will be within the first operational year of the Project.
- 7.3 All measures undertaken by both the Contractor and the specialist Landscape Sub-Contractor during the construction phase and first year of the operational phase shall be audited by a Registered Landscape Architect (RLA), as a member of the Environmental Team (ET), on a regular basis to ensure compliance with the intended aims of the measures. To fulfil the aforementioned requirements, on-site landscape and visual mitigation measures were audited by

RLA in the reporting month.

- 7.4 According to Section 7.3.1.2 of the EM&A Manual (AEIAR-174/2013), site audits shall be undertaken at least once every two weeks throughout the construction period to monitor and audit the timely implementation of landscape and visual mitigation measures within the site boundaries of this Project.
- 7.5 The broad scope of the audit is detailed below but should also be undertaken with reference to the more specific checklist provided in **Table 7.2**. The summaries of site audits are attached in **Appendix I**:
 - The extent of the agreed works areas should be regularly checked during the construction phase. Any trespass by the Contractor outside the limit of the works, including any damage to existing trees and soft landscape areas shall be prohibited;
 - the progress of the engineering works should be regularly reviewed on site to identify the earliest practical opportunities for the landscape works to be undertaken;
 - all existing trees and vegetation within the study area which are not directly affected by the works are retained and protected;
 - the methods of protecting existing vegetation proposed by the Contractor are acceptable and enforced;
 - preparation, lifting transport and re-planting operations for any transplanted trees;
 - all landscaping works are carried out in accordance with the specifications;
 - the planting of new trees, shrubs, groundcover, climbers, ferns, grasses and other plans, together with the replanting of any transplanted trees are carried out properly and within the right season; and
 - all necessary horticultural operations and replacement planting are undertaken throughout the Establishment Period to ensure the healthy establishment and growth of both transplanted trees and all newly established plants.

Table 7.2 Construction Phase Audit Checklist for Landscape and Visual Mitigation Measures

Area of Works	Items to be Monitored
Advance planting	Monitoring of implementation and maintenance of planting, and against possible incursion, physical damage, fire, pollution, surface erosion, etc.

Area of Works	Items to be Monitored	
Protection of all trees and existing soft landscape areas to be retained	Identification and demarcation of trees / vegetation to be retained, erection of physical protection (e.g. fencing), monitoring against possible incursion, physical damage, fire, pollution, surface erosion, etc.	
Clearance of existing vegetation	Identification and demarcation of trees / vegetation to be cleared, checking of extent of works to minimise damage, monitoring of adjacent areas against possible incursion, physical damage, fire, pollution, surface erosion, etc.	
Pruning of trees	Identification and demarcation of trees / vegetation to be pruned, monitoring of extent of pruning to minimise damage, timing of operations, implementation of all stages of preparatory and pruning works, and maintenance of pruned vegetation, etc.	
Plant supply	Monitoring of operations relating to the supply of specialist plant material (including the collecting, germination and growth of plants from seed) to ensure that plants will be available in time to be used within the construction works.	
Soiling, planting, etc.	Monitoring of implementation and maintenance of soiling and planting works and against possible incursion, physical damage, fire, pollution, surface erosion, etc.	
Site fencing and hoarding	Implementation and maintenance, to ensure compliance with agreed designs and check that it matches the surrounding environment and does not cause visual intrusion.	
Architectural treatment of engineering works.	Implementation and maintenance of mitigation measures, to ensure compliance with agreed designs as applicable.	
Establishment Works	Monitoring of implementation of maintenance operations during Establishment Period.	

- 7.6 In the event of non-compliance the responsibilities of the relevant parties is detailed in the Event / Action plan attached in **Appendix J**.
- 7.7 In the reporting month, no non-compliance of the landscape and visual mitigation measures was recorded by RLA.

8 CULTURAL HERITAGE

- 8.1 According to Section 8.3.1.1 of EM&A Manual (AEIAR-174/2013), as a precautionary measure, it is recommended that if any antiquity or supposed antiquity is discovered during the course of the excavation works undertaken by the Contractor, the discovery shall be reported to the AMO immediately and all necessary measures taken to preserve it.
- 8.2 According to Section 8.3.1.2 of EM&A Manual (AEIAR-174/2013), no EM&A is required during the construction and operational phase.

9 WASTE MANAGEMENT

- 9.1 According to Section 9.3.1.1 of EM&A Manual (AEIAR-174/2013), the effective management of waste arisings during the construction phase will be monitored through the site audit programme. Regular audits and site inspections should be carried out by the Engineer, ET and Contractor to ensure that the recommended good site practices and other mitigation measures are implemented by the Contractor. The summaries of site audits are attached in **Appendix I**.
- 9.2 According to Sections 9.3.1.3 and 9.3.1.4 of EM&A Manual (AEIAR-174/2013), documents including licenses, permits, disposal and recycling records should be reviewed and audited during site audits for the compliance with the legislation and contract requirements to ensure proper records are being maintained and procedures undertaken in accordance with the Waste Management Plan.
- 9.3 With reference to the relevant handing records of this Project, the quantities of different types of waste generated in the reporting month are summarized and presented in the **Appendix O**.

10 ENVIRONMENTAL AUDIT

Site Audits

- 10.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix I**.
- 10.2 Site audits were conducted on 02, 09, 16, 23 and 30 June 2022 in the reporting month. Site inspection of the IEC was conducted on 16 June 2022. No non-compliance was observed during the site audit.

Implementation Status of Environmental Mitigation Measures

- 10.3 According to Environmental Permits, the approved EIA Reports (Register No.: AEIAR-174/2013 and AEIAR-173/2013), and the EM&A Manuals of the Project (AEIAR-174/2013 and AEIAR-173/2013), the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An Environmental Mitigation Implementation Schedule (EMIS) is provided in **Appendix K**.
- 10.4 The ET weekly site inspections were carried out during the reporting month and the observations and recommendations are summarized in **Table 10.1**. Refer to **Appendix I** for the site inspection summary reports in the reporting month.

Table 10.1 Observations and Recommendations of Site Audit

Parameters	Date	Observations and Recommendations	Follow-up	
Air Quality	02 June 2022	Stockpile of dusty material (e.eg. bags of cement and excavated mud) shall be covered by impervious sheet on top as a dust suppression measures	Stockpile of excavated mud was covered and bags of cement were removed.	
		NRMM labels shall be displayed on regulated machines	NRMM labels were displayed.	
Noise	26 May 2022	Noise mitigation measures shall be implemented on site to minimize the noise generated from breaking activities.	Breaker was removed	
Water Quality	N/A	There was no observation in the reporting period.	N/A	
Ecology	N/A	There was no observation in the reporting period.	N/A	
Landscape and Visual	N/A	There was no observation in the reporting period.	N/A	

Parameters	Date	Observations and Recommendations	Follow-up	
Waste / Chemical Management	09 June 2022	Contractor is reminded to provide drip tray to prevent accidentally leakage of oil during chemical handling	Oil bottles were removed.	
Permits /Licences	N/A	There was no observation in the reporting period.	N/A	

Implementation Status of Event and Action Plans

10.5 The Event and Action Plans for air quality, construction noise, and landscape and visual are presented in **Appendix J**.

Air Quality Monitoring

• No Action and Limit Level exceedance for 24-hour TSP monitoring was recorded.

Construction Noise Monitoring

• No Action / Limit Level exceedance was recorded in the reporting month.

Landscape and Visual

• No landscape and visual non-conformity was recorded.

Status of Required Submission under Environmental Permit

10.6 According the Section 11.3.2.1 (c) of the EM&A Manual (AEIAR-174/2013), status of required submission under EP-451/2013 during the reporting period are summarized in **Table 10.2**.

Table 10.2 Status of Required Submission under Environmental Permit

EP Condition	Submission	Submission Date			
EP-451/2013					
Condition 2.3	Management Organization of Main Construction Companies	20 January 2020			
Condition 2.4	Design Drawing of the Project	20 January 2020			
Condition 2.5	Landscape Mitigation Plan(s)	7 May 2020			
Condition 2.10 (a)	Supplementary Contamination Assessment Plan	18 December 2015			
Condition 2.10 (b)	Supplementary Contamination Assessment Report	6 December 2016			
Condition 3.3	Updated Baseline Monitoring Report	03 November 2020			
Condition 3.4	Monthly EM&A Report (May 2022)	15 June 2022			

11 ENVIRONMENTAL NON-CONFORMANCE

Summary of Complaint, Warning, Notification of any Summons and Successful Prosecution

11.1 The summaries of environmental complaint, warning, summon and notification of successful prosecution for the Project is presented in **Appendix L**.

Summary of Exceedance

- 11.2 The summary of exceedance record in the reporting month is shown in **Appendix M**.
- 11.3 No non-conformity was recorded for landscape and visual inspections conducted in the reporting month.

12 FUTURE KEY ISSUES

Tentative construction programmes for the next three months are provided in **Appendix N**.

- 12.1 Major site activities undertaken for the coming months are summarized as follows:
 - Depressed Road Portal Structure, Capping Beam
 - Depressed Road DPR/SUS connection
 - Cut & Cover Notch construction
 - Westbound TBM Tunnelling
 - Eastbound TBM Tunnelling
 - EB Service Gallery installation
 - ISIG 2 pre-assembly
 - CKL Junction Reinstatement works
 - Road S20 / AMAWBC Road & Drain
 - Road L10 (North) ELS part 2
 - Road L10 (North) RC Structure
 - Road L18 Sheet Pile
 - Outfall 1 Construction
 - District Cooling System (DCS) Section 6B Testing & Commissioning
 - District Cooling System (DCS) Section 7B
 - District Cooling System (DCS) Pipe Jacking ELS
 - District Cooling System (DCS) Pipe Jacking
 - Foot Bridge (FB-02) H Pile Installation
 - Foot Bridge (FB-02) Pier Construction
 - Foot Bridge (FB-02) Bridge Deck Construction
 - CP Tympanum construction
- 12.2 Key environmental issues in the coming months include:
 - Wheel washing bay at site exits;
 - Temporary noise barriers for PMEs;
 - Sedimentation tank for settling muddy water; and
 - Make sure open stockpiles are covered during rainstorm.

Monitoring Schedule

12.3 The tentative environmental monitoring schedule for the next three months are shown in **Appendix B**.

13 CONCLUSIONS AND RECOMMENDATIONS

Conclusions

13.1 This is the 28th Monthly EM&A Report which presents the EM&A works undertaken during the reporting month in accordance with the EM&A Manual (AEIAR-174/2013) and the requirement under EP.

Air Quality Monitoring

13.2 No Action and Limit Level exceedance was recorded for 24-hour TSP monitoring in the reporting month.

Construction Noise Monitoring

- 13.3 No Limit Level exceedance was recorded for day-time construction noise monitoring in the reporting month.
- 13.4 No Action Level exceedance was recorded in the reporting month.

Site Audit

13.5 5 ET joint weekly environmental site inspections were conducted in the reporting month.

Complaint, Notification of Summons and Successful Prosecution

13.6 No environmental complaint was received in the reporting month. No notifications of summons and successful prosecutions were received in the reporting month.

Recommendations

13.7 According to the environmental audit performed in the reporting month, the following recommendations was made:

Construction Noise Impact

• Use of temporary or fixed noise barriers with a surface density of at least 10kg/m² to screen noise from movable and stationary plant.


Air Quality

- NRMM label shall be displayed at a conspicuous position of the regulated machines on site.
- Open stockpiles shall be avoided or covered.
- Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.


Waste / Chemical Management


• All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching the nearby WSRs.


FIGURES

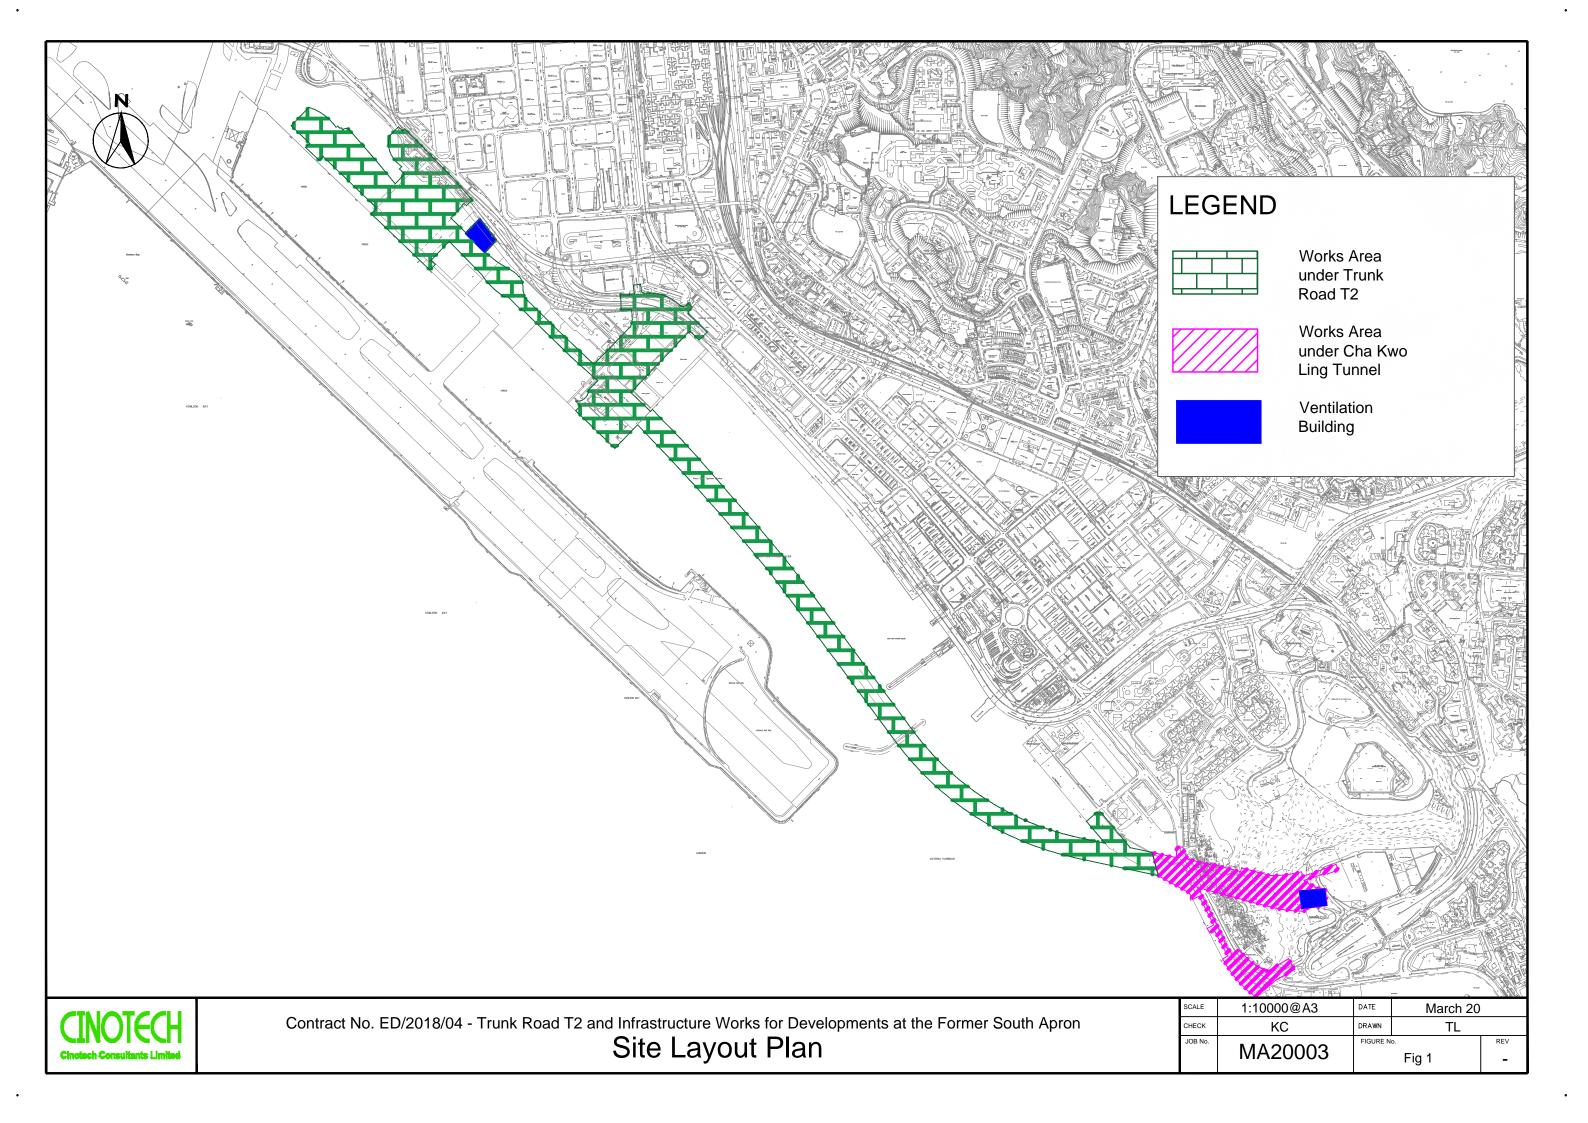




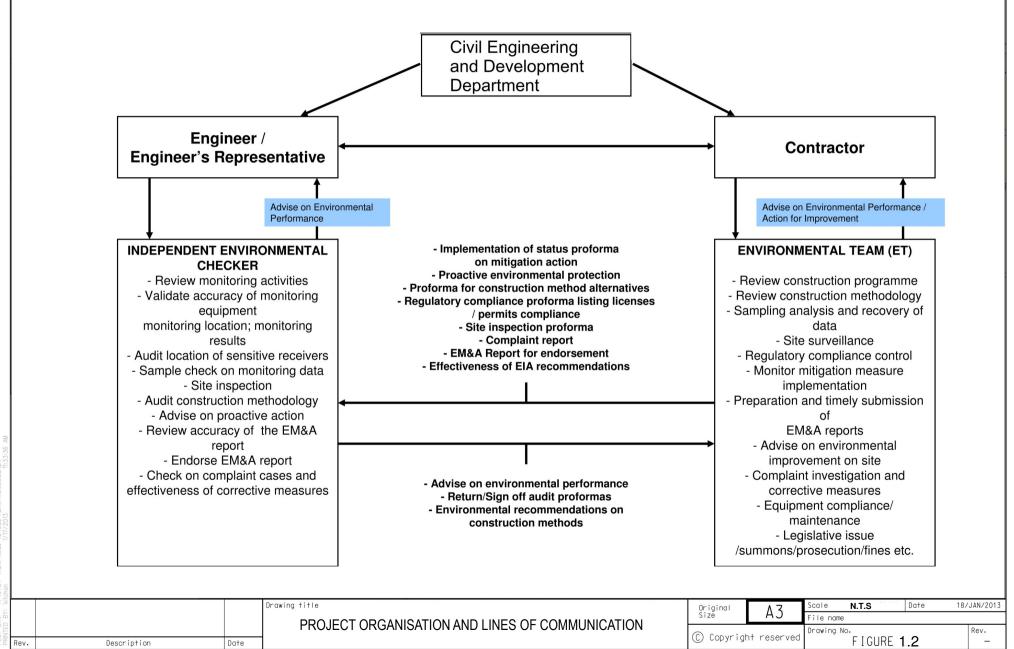

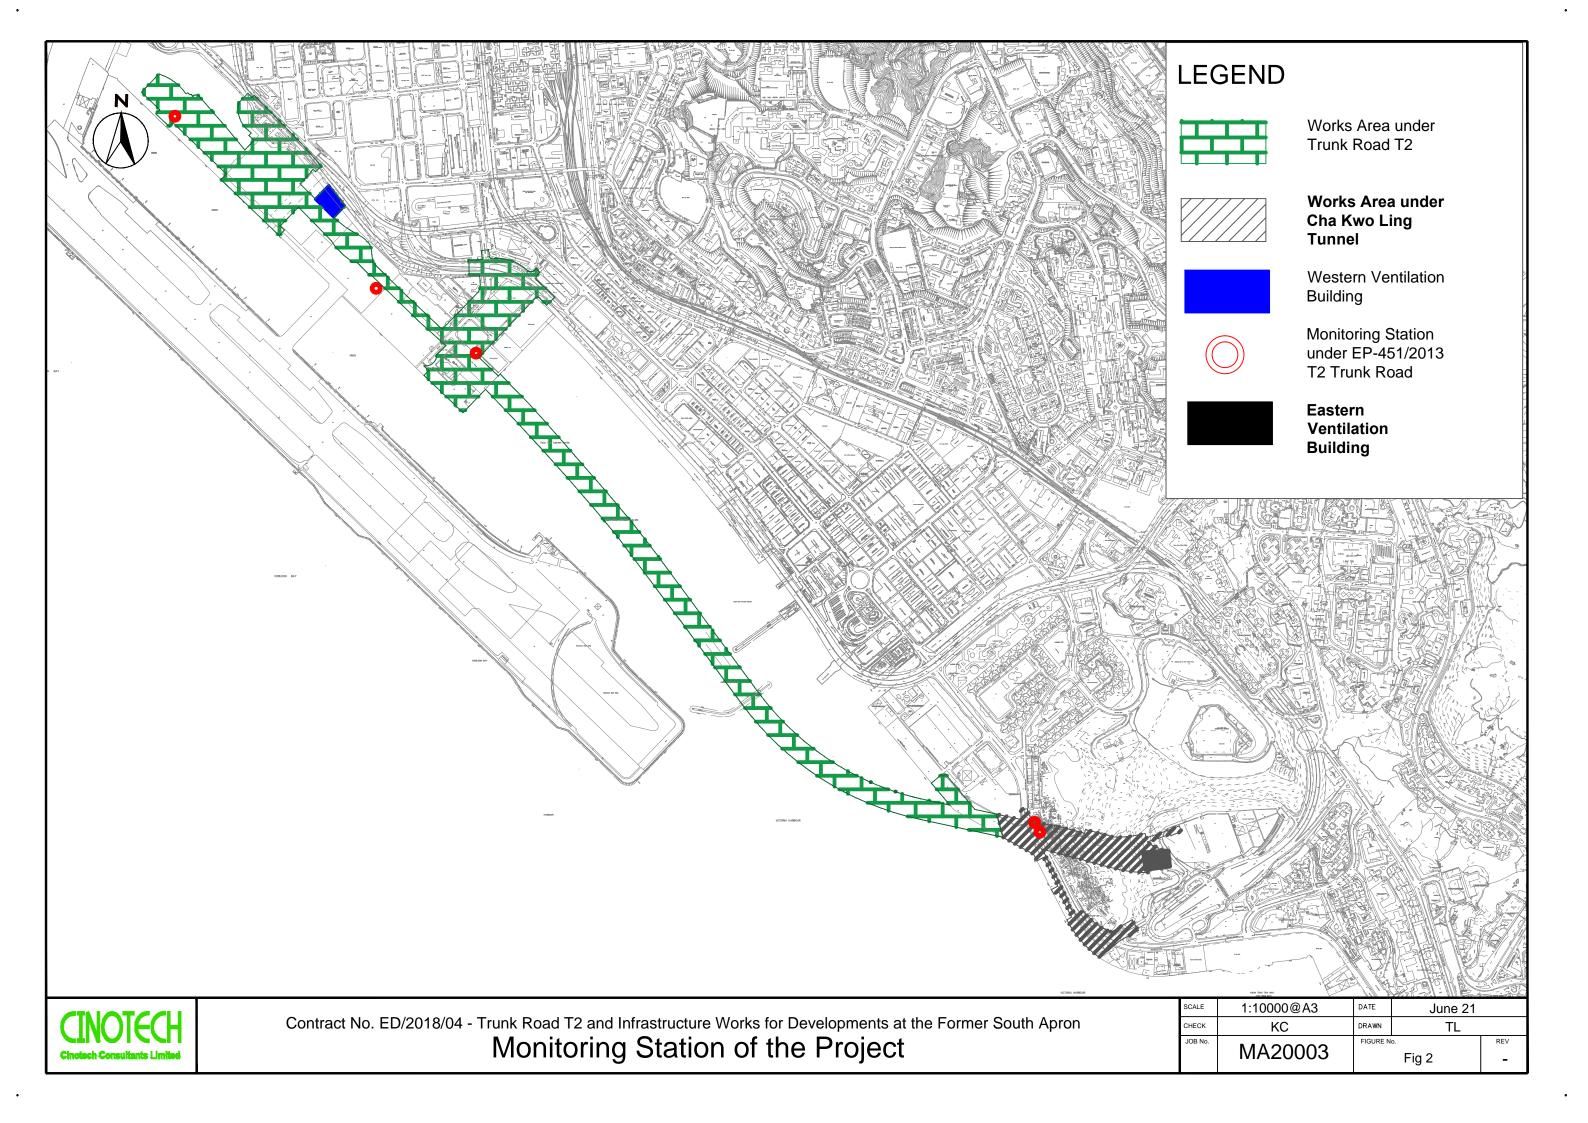

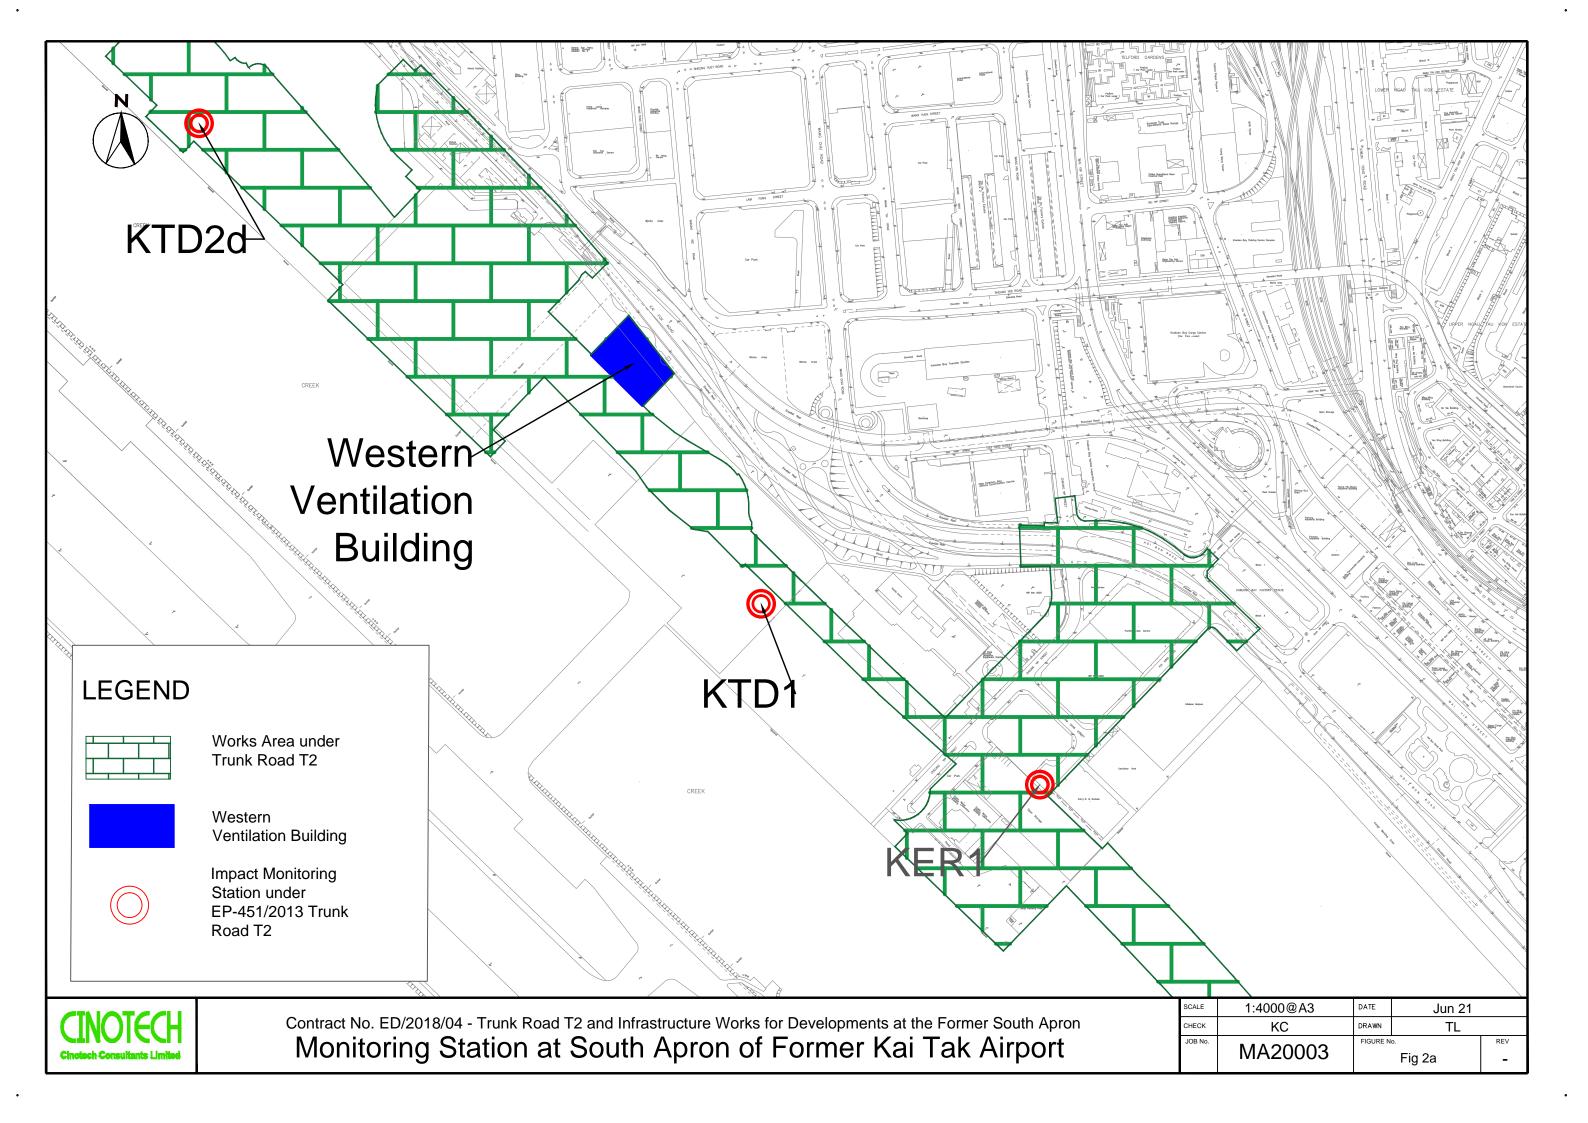

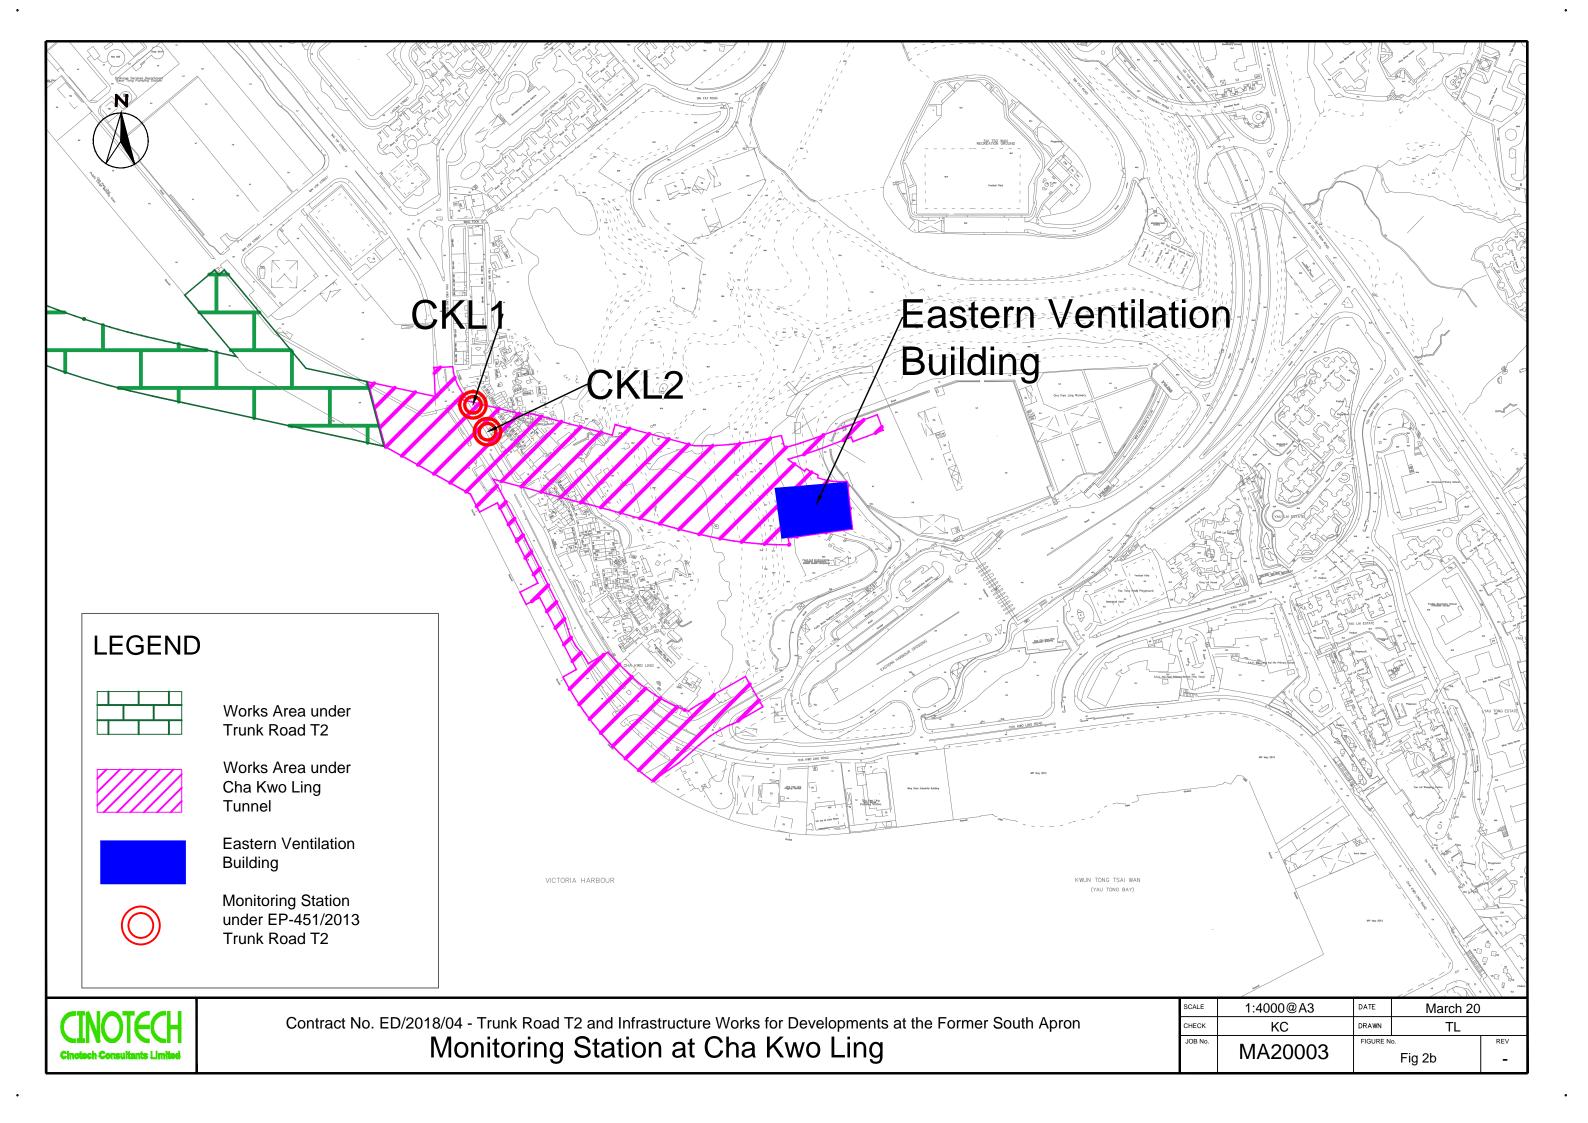

APPENDIX A ACTION AND LIMIT LEVELS

Appendix A - Action and Limit Levels

Table A-1 Action and Limit Levels for 1-hour TSP (in case of complaints)

Location	Action Level, μg/m ³	Limit Level, μg/m ³
KTD1	285	
KTD2d	279	
KER1	295	500
CKL1	323	
CKL2	327	

Table A-2 Action and Limit Levels for 24-hour TSP

Location	Action Level, μg/m ³	Limit Level, μg/m³
KTD1	177	
KTD2d	157	
KER1	172	260
CKL1	191	
CKL2	183	

Table A-3 Action and Limit Levels for Noise during Construction Period

Time Period	Action Level	Limit Level
0700-1900 hrs on normal weekdays	When one documented complaint is received	75 dB(A) ⁽¹⁾

Note:

⁽¹⁾ If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

APPENDIX B ENVIRONMENTAL MONITORING SCHEDULES

Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Impact Air and Noise Monitoring Schedule (June 2022)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			1-Jun	2-Jun	3-Jun	4-Jun
						24-hr TSP
5-Jun	6-Jun	7-Jun	8-Jun	9-Jun	10-Jun	11-Jun
	Noise			24-hr TSP		
12-Jun	13-Jun	14-Jun	15-Jun	16-Jun	17-Jun	18-Jun
		24-hr TSP	Noise			
19-Jun	20-Jun	21-Jun	22-Jun	23-Jun	24-Jun	25-Jun
	24-hr TSP	Noise				24-hr TSP
26-Jun	27-Jun	28-Jun	29-Jun	30-Jun		
	Noise		24-hr TSP			

The schedule may be changed due to unforeseen circumstances (adverse weather, safety concerns, etc.)

Air Quality Monitoring Station

24-hr TSP

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

KER1 - Future Residential Development at Kerry Godown

CKL1 - Flat 121 Cha Kwo Ling Village

CKL2 - Flat 103 Cha Kwo Ling Village

Noise Monitoring Station

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KER1 - Future Residential Development at Kerry Godown

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

CKL1 - Flat 121 Cha Kwo Ling Village

^{*}Noise: Noise Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

^{**24-}hr TSP:24-hr TSP Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Tentative Impact Air and Noise Monitoring Schedule (July 2022)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	•	•	•		1-Jul	2-Jul
3-Jul	4-Jul	5-Jul	6-Jul	7-Jul	8-Jul	9-Jul
		24-hr TSP	Noise			24-hr TSP
10-Jul	11-Jul	12-Jul	13-Jul	14-Jul	15-Jul	16-Jul
	Noise		24-hr TSP			
17-Jul	18-Jul	19-Jul	20-Jul	21-Jul	22-Jul	23-Jul
		24-hr TSP	Noise			
24-Jul	25-Jul	26-Jul	27-Jul	28-Jul	29-Jul	30-Jul
	24-hr TSP	Noise				24-hr TSP
31-Jul						

The schedule may be changed due to unforeseen circumstances (adverse weather, safety concerns, etc.)

Air Quality Monitoring Station

24-hr TSP

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

KER1 - Future Residential Development at Kerry Godown

CKL1 - Flat 121 Cha Kwo Ling Village

CKL2 - Flat 103 Cha Kwo Ling Village

Noise Monitoring Station

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KER1 - Future Residential Development at Kerry Godown

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

CKL1 - Flat 121 Cha Kwo Ling Village

^{*}Noise: Noise Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

^{**24-}hr TSP:24-hr TSP Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Tentative Impact Air and Noise Monitoring Schedule (August 2022)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Aug	2-Aug	3-Aug	4-Aug	5-Aug	6-Aug
				24-hr TSP	Noise	
7-Aug	8-Aug	9-Aug	10-Aug	11-Aug	12-Aug	13-Aug
			24-hr TSP	Noise		
14-Aug	15-Aug	16-Aug	17-Aug	18-Aug	19-Aug	20-Aug
		24-hr TSP	Noise			
21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	26-Aug	27-Aug
	24-hr TSP	Noise				24-hr TSP
28-Aug	29-Aug	30-Aug	31-Aug			
	Noise					

The schedule may be changed due to unforeseen circumstances (adverse weather, safety concerns, etc.)

Air Quality Monitoring Station

24-hr TSP

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

KER1 - Future Residential Development at Kerry Godown

CKL1 - Flat 121 Cha Kwo Ling Village

CKL2 - Flat 103 Cha Kwo Ling Village

Noise Monitoring Station

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KER1 - Future Residential Development at Kerry Godown

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

CKL1 - Flat 121 Cha Kwo Ling Village

^{*}Noise: Noise Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

^{**24-}hr TSP:24-hr TSP Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Tentative Impact Air and Noise Monitoring Schedule (September 2022)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1-Sep	2-Sep	3-Sep
					24-hr TSP	
4-Sep	5-Sep	6-Sep	7-Sep	8-Sep	9-Sep	10-Sep
				24-hr TSP	Noise	
11-Sep	12-Sep	13-Sep	14-Sep	15-Sep	16-Sep	17-Sep
			24-hr TSP	Noise		
18-Sep	19-Sep	20-Sep	21-Sep	22-Sep	23-Sep	24-Sep
		24-hr TSP	Noise			
25-Sep	26-Sep	27-Sep	28-Sep	29-Sep	30-Sep	
	24-hr TSP	Noise			24-hr TSP	
	2 101	- 19-9-			2.11.101	

The schedule may be changed due to unforeseen circumstances (adverse weather, safety concerns, etc.)

Air Quality Monitoring Station

24-hr TSP

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

KER1 - Future Residential Development at Kerry Godown

CKL1 - Flat 121 Cha Kwo Ling Village

CKL2 - Flat 103 Cha Kwo Ling Village

Noise Monitoring Station

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KER1 - Future Residential Development at Kerry Godown

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

CKL1 - Flat 121 Cha Kwo Ling Village

^{*}Noise: Noise Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

^{**24-}hr TSP:24-hr TSP Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

APPENDIX C COPIES OF CALIBRATION CERTIFICATES FOR AIR QUALITY MONITORING

High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET



						File No. N	1A20003/18/0014
Project No.	CKL 1 - Flat 12	21 Cha Kwo Ling	Village			_	
Date:	5-M	Iay-22 Next Due Date: 5-Jul-22		Operator:	SK		
Equipment No.:)1-18	_		E 5170	-	
1 1			-			·	
			Ambient	Condition			
Temperatu	re, Ta (K)	297.2	Pressure, Pa	ı (mmHg)		759.3	
g : 1	127		rifice Transfer Sta				0.02420
Serial		3864	Slope, mc	0.05922	Intercep oc = $[\Delta H \times (Pa/76)]$		-0.02420
Last Calibra		31-Jan-22			к (Pa/760) x (298		
Next Calibr	ation Date:	31-Jan-23		Qstu = {[ΔII 2	X (F a/ / 00) X (290	/1a)] -DC}/III	
		•	Calibration of	f TSP Sampler			
Colibration		Or	·fice	1		HVS	
Calibration Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	50) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of water	· ·) x (298/Ta)] ^{1/2} Y axis
1	13.2		3.64	61.81	10.2	,	3.20
2	10.4		3.23	54.91	8.3	,	2.88
3	8.7		2.95	50.26	6.1	,	2.47
4	6.4	:	2.53	43.17	4.3		2.08
5	3.7		1.93	32.92	2.0		1.42
By Linear Regr Slope , mw =	ression of Y on 2	X		Intercept, bw :	-0.640) 5	
Correlation	coefficient* =	0.	.9975	_			
*If Correlation C	Coefficient < 0.9	90, check and rec	calibrate.	_			
- 4 map n		0		Calculation			
		Curve, take Qstd					
From the Regres	ssion Equation, t	he "Y" value acco	ording to				
		mw x ($\mathbf{Qstd} + \mathbf{bw} = [\Delta \mathbf{W}]$	x (Pa/760) x (2	$[298/Ta)]^{1/2}$		
FF1 6 G			2 (55) (5)	T. (200)			
Therefore, Se	et Point; $W = (n$	nw x Qstd + bw)	² x (760 / Pa) x (Ta / 298) =	4.22		
Remarks:							
				h	1		
Conducted by:	Wong Sl	ning Kwai	Signature	·	<u>/\-</u>	Date:	5-May-22
				1 -	γ. s. r		
Checked by:	Henry	Leung	Signature:	\-le-	, Don	Date:	5-May-22

High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET



File No. MA20003/55/0014

Project No.	CKL 2 - Flat 103	3 Cha Kwo Ling	Village			•	
Date:	5-Ma	ny-22	Next Due Date:	:5-Jul-22		Operator:	SK
Equipment No.:	A-0	1-55	Model No.:	TE	E 5170	Serial No.	1956
			Ambient C	ondition			
Temperatur	re, Ta (K)	297.2	Pressure, Pa			759.3	
•	, , ,		,	<i>\</i>			
		Or	ifice Transfer Star	ndard Informa	ntion		
Serial	No.	3864	Slope, mc	0.05922	Intercept	t, bc	-0.02420
Last Calibra	ation Date:	31-Jan-22	r	nc x Qstd + bo	$c = [\Delta H \times (Pa/760)]$) x (298/Ta)] ¹	/2
Next Calibra	ation Date:	31-Jan-23	•	$Qstd = \{ [\Delta H \ x] \}$	(Pa/760) x (298/7	Γa)] ^{1/2} -bc} / n	ıc
			Calibration of T	ΓSP Sampler			
Calibration		Or	fice			HVS	
Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	50) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of water		(60) x (298/Ta)] ^{1/2} Y-axis
1	13.1		3.62	61.58	10.1		3.18
2	11.1		3.33	56.72	7.8		2.80
3	8.8		2.97	50.55	6.2		2.49
4	5.5		2.35	40.05	3.5		1.87
5	3.1		1.76	30.17	2.0		1.42
Slope , mw = Correlation	ession of Y on X 0.0555 coefficient* = Coefficient < 0.99	0	.9972	-	-0.304		
From the TSP Fi	eld Calibration C	urve_take Ostd		ilculation			
	sion Equation, th	_					
rioni die Regies	sion Equation, th	e i value acco	ording to				
		mw x Q	$\mathbf{Qstd} + \mathbf{bw} = [\mathbf{\Delta W} \ \mathbf{x}]$	(Pa/760) x (29	98/Ta)] ^{1/2}		
Therefore, Se	et Point; W = (m	w x Qstd + bw)	² x (760 / Pa) x (7	Ta / 298) =	4.34		
Remarks:							
Conducted by:	Wong Sh	ing Kwai	Signature:	K	<u> </u>	Date:	5-May-22
Checked by:	Henry	Leung	Signature:	\-lan	1 Xon	Date:	5-May-22

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET



File No. MA20003/04/0012

Project No.	KER 1 - Future		_				
Date:	11-May-22		11-May-22 Next Due Date: 11-Jul-22		-Jul-22	Operator:	
Equipment No.:			_	TE	E 5170	Serial No.	10595
			Ambient C	ondition			
Temperatur	re, Ta (K)	298	Pressure, Pa			755.7	
	, , , ,			<i>\ \ \ \ \ \ \ \ \ \</i>			
		Or	ifice Transfer Star	ndard Informa	ation		
Serial	No.	3864	Slope, mc	0.05922	Intercept	t, bc	-0.02420
Last Calibra	ntion Date:	31-Jan-22			$c = [\Delta H \times (Pa/760]]$		
Next Calibra	ation Date:	31-Jan-23		$Qstd = \{ [\Delta H \ x] \}$	(Pa/760) x (298/7	Γa)] ^{1/2} -bc} / m	c
			Calibration of	TSP Sampler			
Calibration		Or	fice	T		HVS	
Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	50) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of water		50) x (298/Ta)] ^{1/} -axis
1	13.3		3.64	61.82	9.7	3.11	
2	10.6		3.25	55.23	7.3	2.69	
3	8.4		2.89	49.21	5.8	2.40	
4	5.4		2.32	39.54	3.3	1.81	
5	3.2		1.78	30.53	2.1		1.45
By Linear Regr Slope , mw =		(]	Intercept, bw :	-0.240)2	
	coefficient* =	- 0	.9976	1 1, 1			
*If Correlation C				•			
			Set Point Ca	alculation			
From the TSP Fi	eld Calibration C	Curve, take Qstd					
From the Regress	sion Equation, th	e "Y" value acco	ording to				
_	-		-		1/2		
		mw x ($\mathbf{Qstd} + \mathbf{bw} = [\mathbf{\Delta W} \ \mathbf{x}]$	(Pa/760) x (29	98/Ta)] ^{1/2}		
Therefore, Se	et Point; W = (m	w x Qstd + bw)	² x (760 / Pa) x (7	Γa / 298) =	4.28		
Remarks:							
a			~.	X)	λ	-	44.35
Conducted by:	Wong Sh	ing Kwai	Signature:			Date:	11-May-22
Checked by	Henry	Leung	Signature:	1-0	- Mari	Data	11-May-22

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET



File No. MA20003/44/0013

Project No.	Io. KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)						
Date:	11-M	lay-22	Next Due Date:	11-	-Jul-22	Operator:	SK
Equipment No.:	A-0	01-44	Model No.:	TE	E-5170	Serial No.	1316
			Ambient C	ondition			
Temperatu	re, Ta (K)	298	Pressure, Pa			755.7	
		Or	ifice Transfer Star	ndard Informa	ation		
Serial	No.	3864	Slope, mc	0.05922	Intercept		-0.02420
Last Calibra	ation Date:	31-Jan-22			$c = [\Delta H \times (Pa/760)]$		
Next Calibra	ation Date:	31-Jan-23	($Qstd = \{ [\Delta H \ x] $	(Pa/760) x (298/7	Γa)] ^{1/2} -bc} / m	ıc
	I		Calibration of 7	TSP Sampler	T		
Calibration	ΔH (orifice),		fice	Ostd (CEM)	AM (IBIO) :	HVS	(0) (200 /FL) 1/
Point	in. of water	[ΔH x (Pa/76	$(50) \times (298/\text{Ta})^{1/2}$	Qstd (CFM) X - axis	Δ W (HVS), in. of water		60) x (298/Ta)] ^{1/} /-axis
1	13.2		3.62	61.59	9.9		3.14
2	11.1		3.32	56.51	7.6		2.75
3	8.6		2.92	49.79	5.7	2.38	
4	5.8		2.40	40.96	3.5	1.87	
5	3.3		1.81	31.00	1.9		1.37
	0.0570 coefficient* =		.9978	Intercept, bw :	-0.433	32	
*If Correlation C	Coefficient < 0.9	90, check and rec	ealibrate.				
			Set Point Ca	alculation			
From the TSP Fi	eld Calibration (Curve, take Qstd					
From the Regres	sion Equation, tl	ne "Y" value acco	ording to				
-		_		(B) (F) (C)	20/m \2-1/2		
		mw x Q	$\mathbf{Qstd} + \mathbf{bw} = [\Delta \mathbf{W} \ \mathbf{x}]$	(Pa/760) x (29	98/Ta)]" ²		
Therefore, Se	et Point; W = (n	nw x Qstd + bw)	2 x (760 / Pa) x (7	Γa / 298) =	4.10		
Remarks:							
				h			
Conducted by:	Wong Sl	ning Kwai	Signature:		<u> </u>	Date:	11-May-22
				1 0			
Checked by:	Henry	Leung	Signature:	1-Pa	2 Xon	Date:	11-May-22

High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET



File No. MA20003/41/0012

						_	
Project No.	KTD 2D - Next	to the SOR Offic	ce of Trunk Road T	2 in Kai Tak A	area		
Date:	11-M	1ay-22	Next Due Date:	11-	-Jul-22	Operator:	SK
Equipment No.:					E 5170	Serial No.	5280
			•			_	
			Ambient C	ondition			
Temperatu	re, Ta (K)	298	Pressure, Pa	(mmHg)		755.7	
		Or	ifice Transfer Star	ndard Informa	ation		
Serial	No.	3864	Slope, mc	0.05922	Intercept		-0.02420
Last Calibra	ation Date:	31-Jan-22			$c = [\Delta H \times (Pa/760]]$		
Next Calibra	ation Date:	31-Jan-23		$Qstd = \{ [\Delta H \ x]$	(Pa/760) x (298/7	Γa)] ^{1/2} -bc} / n	ıc
	<u> </u>		Calibration of	ISP Sampler	I		
Calibration	ATT ('C')	Or	fice	O . 1 (CF) ()		HVS	(200 TT) 1/2
Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	$(50) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	ΔW (HVS), in. of water		(60) x (298/Ta)] ^{1/2} Y-axis
1	13.3		3.64	61.82	10.1		3.17
2	10.5		3.23	54.97	8.3		2.87
3	8.7		2.94	50.07	6.1		2.46
4	6.3		2.50 42.67		4.3		2.07
5	3.5		1.87	31.91	2.2		1.48
By Linear Regr Slope , mw = Correlation *If Correlation C	0.0577 coefficient* =	_	.9973	Intercept, bw	-0.376	66	
			Set Point Ca	alculation			
From the TSP Fi	eld Calibration	Curve, take Qstd					
From the Regres	sion Equation, th	he "Y" value acco	ording to				
C			· ·		1/0		
		mw x C	$\mathbf{Qstd} + \mathbf{bw} = [\mathbf{\Delta W} \ \mathbf{x}]$	(Pa/760) x (29	98/Ta)] ^{1/2}		
Therefore Se	et Point· W – (n	nw v Ostd + hw)	² x (760 / Pa) x (7	Га / 298) —	4.46		
Therefore, 50	λι 1 Omi, w = (n	iw x Qsia + bw)	X (700/1a) X (1 a / 2 / 0) =	4.40		
Remarks:							
Conducted by:	Wong Sl	hing Kwai	Signature:	K	<u></u>	Date:	11-May-22
a			α.	\ 0	2 X27	_	44.34
Checked by:	Henry	Leung	Signature:	- ten	7 may	Date:	11-May-22
					,		





RECALIBRATION DUE DATE:

January 31, 2023

Certificate of Calibration

Calibration Certification Information

Cal. Date: January 31, 2022

Rootsmeter S/N: 438320

Ta: 294 **Pa:** 752.6

°K

Operator: Jim Tisch

ım iiscn

mm Hg

Calibration Model #: TE-5025A Calibrator S/N: 3864

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4490	3.2	2.00
2	3	4	1	1.0320	6.4	4.00
3	5	6	1	0.9160	7.9	5.00
4	7	8	1	0.8730	8.8	5.50
5	9	10	1	0.7230	12.7	8.00

	Data Tabulation								
Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right) \left(\frac{Tstd}{Ta}\right)}$		Qa	√∆H(Ta/Pa)				
(m3)	(x-axis)	(y-axis)	Va	(x-axis)	(y-axis)				
0.9995	0.6898	1.4169	0.9957	0.6872	0.8839				
0.9952	0.9643	2.0037	0.9915	0.9608	1.2500				
0.9932	1.0843	2.2402	0.9895	1.0802	1.3976				
0.9920	1.1363	2.3496	0.9883	1.1321	1.4658				
0.9868	1.3649	2.8337	0.9831	1.3598	1.7678				
	m=	2.09281		m=	1.31048				
QSTD	b=	-0.02426	QA [b=	-0.01514				
	r=	0.99993	,	r=	0.99993				

	Calculatio	ns		
$Vstd= \Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta) Va= \Delta Vol((Pa-\Delta P)/Pa)$		ΔVol((Pa-ΔP)/Pa)		
Qstd=	Vstd/∆Time	Qa= Va/ΔTime		
	For subsequent flow ra	te calculatio	ns:	
Qstd=	$1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b\right)$	Qa=	$1/m\left(\left(\sqrt{\Delta H(Ta/Pa)}\right)-b\right)$	

	Standard Conditions
Tstd:	298.15 °K
Pstd:	760 mm Hg
	Key
ΔH: calibrate	or manometer reading (in H2O)
ΔP: rootsme	ter manometer reading (mm Hg)
Ta: actual ab	solute temperature (°K)
Pa: actual ba	rometric pressure (mm Hg)
b: intercept	
m: slope	

RECALIBRATION

US EPA recommends annual recalibration per 1998
40 Code of Federal Regulations Part 50 to 51,
Appendix B to Part 50, Reference Method for the
Determination of Suspended Particulate Matter in
the Atmosphere, 9.2.17, page 30

illage of Cleves, OH 45002

www.tisch-env.com

TOLL FREE: (877)263-7610

FAX: (513)467-9009



Certificate of Calibration - Wind Monitoring Station

Description: Yau Lai Estate, Bik Lai House

Manufacturer: <u>Davis Instruments</u>

Model No.: <u>Davis7440</u>

Serial No.: <u>MC01010A44</u>

Equipment No.: <u>SA-03-04</u>

Date of Calibration <u>19-Feb-2022</u>

Next Due Date <u>19-Aug-2022</u>

1. Performance check of Wind Speed

Wind Sp	peed, m/s	Difference D (m/s)		
Wind Speed Reading (V1) Anemometer Value (V2)		D = V1 - V2		
0.0 0.0		0.0		
1.5	1.5	0.0		
2.5	2.5	0.0		
4.2	4.3	-0.1		

2. Performance check of Wind Direction

Wind Di	rection (°)	Difference D (°)		
Wind Direction Reading (W1)	Marine Compass Value (W2)	D = W1 - W2		
0	0	0.0		
90	90	0.0		
180	180	0.0		
270	270	0.0		

Test Specification:

- 1. Performance Wind Speed Test The wind meter was on-site calibrated against the anemometer
- 2. Performance Wind Direction Test The wind meter was on-site calibrated against the marine compass at four direction

Calibrated by: Approved by: Approved by: Henry Leung

APPENDIX D WEATHER INFORMATION

Appendix D - Weather Conditions During Impact Monitoring Period

Date	Mean Air Temperature $(^{\circ}C)^{1}$	Mean Relative Humidity	Precipitation (mm) ³
		(%) ²	
1-Jun-22	28.7	81	1.2
2-Jun-22	28.8	80	11.9
3-Jun-22	29.2	81	1.6
4-Jun-22	29.6	78	Trace
5-Jun-22	29.6	78	Trace
6-Jun-22	28.9	83	2.5
7-Jun-22	27.4	86	33.8
8-Jun-22	25.8	93	66.0
9-Jun-22	26.3	90	28.7
10-Jun-22	26.1	92	25.8
11-Jun-22	26.8	89	47.5
12-Jun-22	28.4	84	2.6
13-Jun-22	28.9	80	0.0
14-Jun-22	27.4	87	42.8
15-Jun-22	26.7	88	11.0
16-Jun-22	27.6	84	2.6
17-Jun-22	29.0	79	1.0
18-Jun-22	28.8	81	1.3
19-Jun-22	29.3	81	0.1
20-Jun-22	29.2	80	2.8
21-Jun-22	29.4	80	Trace
22-Jun-22	29.5	78	0.0
23-Jun-22	30.0	74	0.0
24-Jun-22	30.0	73	0.0
25-Jun-22	29.6	74	0.0
26-Jun-22	30.0	74	0.3
27-Jun-22	30.1	73	0.1
28-Jun-22	30.6	71	0.0
29-Jun-22	30.2	78	0.7
30-Jun-22	27.5	89	64.9

(Reporting Month: June 2022)

Remarks:

Source - Hong Kong Observatory

¹⁻³Retrieved from Manned Weather Station (Hong Kong Observatory) (22°18'07" N, 114°10'27" E)

	June	2022			June	2022	
	Wind Speed a	and Directions		Wind Speed and Directions			
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction
1 Jun 2022	12:00 AM	0.4	NE	2 Jun 2022	3:00 AM	0.4	ENE
1 Jun 2022	1:00 AM	0.4	NE	2 Jun 2022	4:00 AM	1.8	ENE
1 Jun 2022	2:00 AM	0.4	NNE	2 Jun 2022	5:00 AM	1.3	ENE
1 Jun 2022	3:00 AM	0.4	N	2 Jun 2022	6:00 AM	0.9	ENE
1 Jun 2022	4:00 AM	0.4	NNE	2 Jun 2022	7:00 AM	1.3	ENE
1 Jun 2022	5:00 AM	0.9	NNE	2 Jun 2022	8:00 AM	1.8	ENE
1 Jun 2022	6:00 AM	0.0	NNE	2 Jun 2022	9:00 AM	2.2	ENE
1 Jun 2022	7:00 AM	0.0	NNE	2 Jun 2022	10:00 AM	3.1	ENE
1 Jun 2022	8:00 AM	0.4	NNE	2 Jun 2022	11:00 AM	2.7	ENE
1 Jun 2022	9:00 AM	0.4	NNE	2 Jun 2022	12:00 PM	2.7	ENE
1 Jun 2022	10:00 AM	0.9	NNE	2 Jun 2022	1:00 PM	3.1	ENE
1 Jun 2022	11:00 AM	0.9	N	2 Jun 2022	2:00 PM	0.4	ENE
1 Jun 2022	12:00 PM	0.9	NNE	2 Jun 2022	3:00 PM	0.9	ENE
1 Jun 2022	1:00 PM	0.9	NNE	2 Jun 2022	4:00 PM	0.9	ENE
1 Jun 2022	2:00 PM	0.9	NE	2 Jun 2022	5:00 PM	0.9	ENE
1 Jun 2022	3:00 PM	1.8	ENE	2 Jun 2022	6:00 PM	0.9	ENE
1 Jun 2022	4:00 PM	1.8	NE	2 Jun 2022	7:00 PM	0.9	ENE
1 Jun 2022	5:00 PM	0.9	NNE	2 Jun 2022	8:00 PM	1.8	ENE
1 Jun 2022	6:00 PM	0.4	NNE	2 Jun 2022	9:00 PM	1.8	ENE
1 Jun 2022	7:00 PM	0.4	SSE	2 Jun 2022	10:00 PM	0.9	ENE
1 Jun 2022	8:00 PM	0.4	NNE	2 Jun 2022	11:00 PM	0.9	SW
1 Jun 2022	9:00 PM	0.9	NE	3 Jun 2022	12:00 AM	0.9	NNE
1 Jun 2022	10:00 PM	0.4	NE	3 Jun 2022	1:00 AM	1.8	ENE
1 Jun 2022	11:00 PM	1.3	ENE	3 Jun 2022	2:00 AM	1.8	ENE
2 Jun 2022	12:00 AM	2.2	ENE	3 Jun 2022	3:00 AM	1.8	ENE
2 Jun 2022	1:00 AM	1.8	ENE	3 Jun 2022	4:00 AM	3.1	ENE
2 Jun 2022	2:00 AM	0.9	NNE	3 Jun 2022	5:00 AM	0.4	NNE

June 2022				June 2022				
	Wind Speed and Directions				Wind Speed and Directions			
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction	
3 Jun 2022	6:00 AM	0.0	WSW	4 Jun 2022	12:00 PM	1.8	ESE	
3 Jun 2022	7:00 AM	0.4	ESE	4 Jun 2022	1:00 PM	1.3	ESE	
3 Jun 2022	8:00 AM	0.9	SW	4 Jun 2022	2:00 PM	1.3	S	
3 Jun 2022	9:00 AM	1.3	SW	4 Jun 2022	3:00 PM	1.3	SW	
3 Jun 2022	10:00 AM	0.9	NE	4 Jun 2022	4:00 PM	0.9	SW	
3 Jun 2022	11:00 AM	1.3	Е	4 Jun 2022	5:00 PM	1.3	ENE	
3 Jun 2022	12:00 PM	1.3	ENE	4 Jun 2022	6:00 PM	1.3	SW	
3 Jun 2022	1:00 PM	1.8	SW	4 Jun 2022	7:00 PM	0.9	SW	
3 Jun 2022	2:00 PM	1.3	Е	4 Jun 2022	8:00 PM	0.9	NE	
3 Jun 2022	3:00 PM	1.3	ESE	4 Jun 2022	9:00 PM	1.8	ENE	
3 Jun 2022	4:00 PM	1.3	SW	4 Jun 2022	10:00 PM	2.2	ENE	
3 Jun 2022	5:00 PM	1.3	SW	4 Jun 2022	11:00 PM	1.8	ENE	
3 Jun 2022	6:00 PM	0.9	SW	5 Jun 2022	12:00 AM	2.2	ENE	
3 Jun 2022	7:00 PM	0.4	SW	5 Jun 2022	1:00 AM	2.2	ENE	
3 Jun 2022	8:00 PM	0.9	ESE	5 Jun 2022	2:00 AM	2.7	ENE	
3 Jun 2022	9:00 PM	0.9	ESE	5 Jun 2022	3:00 AM	2.2	ENE	
3 Jun 2022	10:00 PM	0.9	SW	5 Jun 2022	4:00 AM	2.2	ENE	
3 Jun 2022	11:00 PM	0.9	SW	5 Jun 2022	5:00 AM	2.2	ENE	
4 Jun 2022	12:00 AM	0.9	ENE	5 Jun 2022	6:00 AM	2.2	ENE	
4 Jun 2022	1:00 AM	1.8	ENE	5 Jun 2022	7:00 AM	1.8	ENE	
4 Jun 2022	2:00 AM	1.8	ENE	5 Jun 2022	8:00 AM	1.8	ENE	
4 Jun 2022	3:00 AM	0.9	Е	5 Jun 2022	9:00 AM	2.2	ENE	
4 Jun 2022	4:00 AM	0.9	ENE	5 Jun 2022	10:00 AM	2.2	ENE	
4 Jun 2022	5:00 AM	1.3	ENE	5 Jun 2022	11:00 AM	1.3	ENE	
4 Jun 2022	6:00 AM	0.9	ENE	5 Jun 2022	12:00 PM	1.3	ENE	
4 Jun 2022	7:00 AM	0.4	SE	5 Jun 2022	1:00 PM	1.3	ESE	
4 Jun 2022	8:00 AM	0.9	SW	5 Jun 2022	2:00 PM	1.3	ENE	
4 Jun 2022	9:00 AM	1.3	ENE	5 Jun 2022	3:00 PM	1.8	ENE	
4 Jun 2022	10:00 AM	1.3	ESE	5 Jun 2022	4:00 PM	1.8	ENE	
4 Jun 2022	11:00 AM	1.3	Е	5 Jun 2022	5:00 PM	2.2	ENE	

June 2022				June 2022			
Wind Speed and Directions				Wind Speed and Directions			
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction
5 Jun 2022	6:00 PM	1.8	ENE	7 Jun 2022	12:00 AM	0.9	ENE
5 Jun 2022	7:00 PM	0.4	ENE	7 Jun 2022	1:00 AM	0.9	ENE
5 Jun 2022	8:00 PM	0.9	ENE	7 Jun 2022	2:00 AM	1.8	ENE
5 Jun 2022	9:00 PM	0.9	ENE	7 Jun 2022	3:00 AM	1.8	ENE
5 Jun 2022	10:00 PM	0.9	ENE	7 Jun 2022	4:00 AM	0.9	ENE
5 Jun 2022	11:00 PM	0.9	ENE	7 Jun 2022	5:00 AM	2.2	ENE
6 Jun 2022	12:00 AM	0.9	ENE	7 Jun 2022	6:00 AM	2.2	ENE
6 Jun 2022	1:00 AM	1.8	ENE	7 Jun 2022	7:00 AM	2.7	ENE
6 Jun 2022	2:00 AM	1.8	ENE	7 Jun 2022	8:00 AM	2.2	ENE
6 Jun 2022	3:00 AM	0.9	ENE	7 Jun 2022	9:00 AM	1.3	Е
6 Jun 2022	4:00 AM	2.7	ENE	7 Jun 2022	10:00 AM	1.8	ENE
6 Jun 2022	5:00 AM	2.2	ENE	7 Jun 2022	11:00 AM	1.8	ESE
6 Jun 2022	6:00 AM	1.8	ENE	7 Jun 2022	12:00 PM	1.3	ENE
6 Jun 2022	7:00 AM	1.8	ENE	7 Jun 2022	1:00 PM	1.3	ESE
6 Jun 2022	8:00 AM	1.8	ENE	7 Jun 2022	2:00 PM	1.8	Е
6 Jun 2022	9:00 AM	2.7	ENE	7 Jun 2022	3:00 PM	1.8	ENE
6 Jun 2022	10:00 AM	2.2	ENE	7 Jun 2022	4:00 PM	1.8	ESE
6 Jun 2022	11:00 AM	1.3	ENE	7 Jun 2022	5:00 PM	1.8	ENE
6 Jun 2022	12:00 PM	3.1	ENE	7 Jun 2022	6:00 PM	1.3	SE
6 Jun 2022	1:00 PM	2.7	ENE	7 Jun 2022	7:00 PM	1.8	ENE
6 Jun 2022	2:00 PM	1.3	ENE	7 Jun 2022	8:00 PM	1.3	ENE
6 Jun 2022	3:00 PM	2.7	ENE	7 Jun 2022	9:00 PM	0.9	ESE
6 Jun 2022	4:00 PM	2.7	ENE	7 Jun 2022	10:00 PM	0.9	Е
6 Jun 2022	5:00 PM	3.1	ENE	7 Jun 2022	11:00 PM	0.9	ENE
6 Jun 2022	6:00 PM	1.3	ENE	8 Jun 2022	12:00 AM	0.9	ENE
6 Jun 2022	7:00 PM	2.7	ENE	8 Jun 2022	1:00 AM	0.4	ESE
6 Jun 2022	8:00 PM	0.4	ENE	8 Jun 2022	2:00 AM	0.9	SE
6 Jun 2022	9:00 PM	0.9	ENE	8 Jun 2022	3:00 AM	1.3	ENE
6 Jun 2022	10:00 PM	0.9	ENE	8 Jun 2022	4:00 AM	0.9	SW
6 Jun 2022	11:00 PM	0.9	ENE	8 Jun 2022	5:00 AM	0.9	ENE

June 2022				June 2022				
	Wind Speed and Directions				Wind Speed and Directions			
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction	
8 Jun 2022	6:00 AM	0.9	Е	9 Jun 2022	12:00 PM	1.8	SW	
8 Jun 2022	7:00 AM	0.4	SW	9 Jun 2022	1:00 PM	0.9	ENE	
8 Jun 2022	8:00 AM	0.9	ENE	9 Jun 2022	2:00 PM	3.1	ENE	
8 Jun 2022	9:00 AM	0.9	ENE	9 Jun 2022	3:00 PM	2.7	ENE	
8 Jun 2022	10:00 AM	1.8	SW	9 Jun 2022	4:00 PM	2.2	ENE	
8 Jun 2022	11:00 AM	0.4	SW	9 Jun 2022	5:00 PM	2.2	ENE	
8 Jun 2022	12:00 PM	0.9	SSW	9 Jun 2022	6:00 PM	2.2	ENE	
8 Jun 2022	1:00 PM	0.9	SW	9 Jun 2022	7:00 PM	0.9	ENE	
8 Jun 2022	2:00 PM	0.9	SW	9 Jun 2022	8:00 PM	0.4	SW	
8 Jun 2022	3:00 PM	1.8	SW	9 Jun 2022	9:00 PM	0.4	NNE	
8 Jun 2022	4:00 PM	0.9	SW	9 Jun 2022	10:00 PM	1.3	ENE	
8 Jun 2022	5:00 PM	0.4	SW	9 Jun 2022	11:00 PM	1.3	ENE	
8 Jun 2022	6:00 PM	0.0	SSE	10 Jun 2022	12:00 AM	1.3	ENE	
8 Jun 2022	7:00 PM	0.9	NE	10 Jun 2022	1:00 AM	1.3	ENE	
8 Jun 2022	8:00 PM	0.4	NE	10 Jun 2022	2:00 AM	1.3	NE	
8 Jun 2022	9:00 PM	0.9	NE	10 Jun 2022	3:00 AM	1.3	ENE	
8 Jun 2022	10:00 PM	0.9	NE	10 Jun 2022	4:00 AM	0.9	ENE	
8 Jun 2022	11:00 PM	0.9	ENE	10 Jun 2022	5:00 AM	1.3	ENE	
9 Jun 2022	12:00 AM	0.9	SW	10 Jun 2022	6:00 AM	1.3	ENE	
9 Jun 2022	1:00 AM	0.4	SSW	10 Jun 2022	7:00 AM	1.8	NE	
9 Jun 2022	2:00 AM	0.9	SW	10 Jun 2022	8:00 AM	2.7	NE	
9 Jun 2022	3:00 AM	0.0	SW	10 Jun 2022	9:00 AM	3.1	NNE	
9 Jun 2022	4:00 AM	0.4	SW	10 Jun 2022	10:00 AM	3.1	N	
9 Jun 2022	5:00 AM	0.4	SW	10 Jun 2022	11:00 AM	2.7	NNE	
9 Jun 2022	6:00 AM	0.9	SW	10 Jun 2022	12:00 PM	1.8	NNE	
9 Jun 2022	7:00 AM	0.0	SSW	10 Jun 2022	1:00 PM	1.3	NNE	
9 Jun 2022	8:00 AM	0.0		10 Jun 2022	2:00 PM	2.7	NNE	
9 Jun 2022	9:00 AM	0.9	NE	10 Jun 2022	3:00 PM	2.2	NNE	
9 Jun 2022	10:00 AM	1.3	ENE	10 Jun 2022	4:00 PM	2.7	NNE	
9 Jun 2022	11:00 AM	2.2	ENE	10 Jun 2022	5:00 PM	3.1	NNE	

June 2022				June 2022				
	Wind Speed a	and Directions			Wind Speed and Directions			
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction	
10 Jun 2022	6:00 PM	2.2	N	12 Jun 2022	12:00 AM	2.2	ENE	
10 Jun 2022	7:00 PM	1.3	NNE	12 Jun 2022	1:00 AM	2.2	ENE	
10 Jun 2022	8:00 PM	2.2	NNE	12 Jun 2022	2:00 AM	2.7	ENE	
10 Jun 2022	9:00 PM	1.8	NE	12 Jun 2022	3:00 AM	2.7	ENE	
10 Jun 2022	10:00 PM	2.2	ENE	12 Jun 2022	4:00 AM	1.8	ENE	
10 Jun 2022	11:00 PM	3.1	NE	12 Jun 2022	5:00 AM	1.3	ENE	
11 Jun 2022	12:00 AM	3.1	ENE	12 Jun 2022	6:00 AM	2.2	ENE	
11 Jun 2022	1:00 AM	3.6	ENE	12 Jun 2022	7:00 AM	1.8	ENE	
11 Jun 2022	2:00 AM	2.7	ENE	12 Jun 2022	8:00 AM	1.8	ENE	
11 Jun 2022	3:00 AM	2.2	ENE	12 Jun 2022	9:00 AM	1.8	ENE	
11 Jun 2022	4:00 AM	2.2	ENE	12 Jun 2022	10:00 AM	0.9	ENE	
11 Jun 2022	5:00 AM	2.2	ENE	12 Jun 2022	11:00 AM	1.3	ENE	
11 Jun 2022	6:00 AM	1.3	ENE	12 Jun 2022	12:00 PM	1.8	ENE	
11 Jun 2022	7:00 AM	1.3	ENE	12 Jun 2022	1:00 PM	1.8	ENE	
11 Jun 2022	8:00 AM	2.2	ENE	12 Jun 2022	2:00 PM	1.3	Е	
11 Jun 2022	9:00 AM	2.7	ENE	12 Jun 2022	3:00 PM	1.3	ESE	
11 Jun 2022	10:00 AM	1.3	Е	12 Jun 2022	4:00 PM	1.3	ENE	
11 Jun 2022	11:00 AM	1.3	ESE	12 Jun 2022	5:00 PM	1.3	ENE	
11 Jun 2022	12:00 PM	1.3	ENE	12 Jun 2022	6:00 PM	0.9	Е	
11 Jun 2022	1:00 PM	1.8	ENE	12 Jun 2022	7:00 PM	0.9	Е	
11 Jun 2022	2:00 PM	1.3	Е	12 Jun 2022	8:00 PM	0.4	ENE	
11 Jun 2022	3:00 PM	1.3	SE	12 Jun 2022	9:00 PM	0.9	SW	
11 Jun 2022	4:00 PM	1.8	ESE	12 Jun 2022	10:00 PM	0.4	SW	
11 Jun 2022	5:00 PM	1.3	Е	12 Jun 2022	11:00 PM	1.3	ENE	
11 Jun 2022	6:00 PM	0.9	ESE	13 Jun 2022	12:00 AM	1.3	NNE	
11 Jun 2022	7:00 PM	0.9	ESE	13 Jun 2022	1:00 AM	0.9	NNE	
11 Jun 2022	8:00 PM	0.9	ESE	13 Jun 2022	2:00 AM	1.3	NE	
11 Jun 2022	9:00 PM	1.3	ENE	13 Jun 2022	3:00 AM	0.4	NNE	
11 Jun 2022	10:00 PM	2.2	ENE	13 Jun 2022	4:00 AM	0.4	NE	
11 Jun 2022	11:00 PM	2.2	ENE	13 Jun 2022	5:00 AM	0.4	NE	

	June	2022		June 2022								
	Wind Speed a	and Directions			Wind Speed a	and Directions						
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction					
13 Jun 2022	6:00 AM	0.4	NNE	14 Jun 2022	12:00 PM	1.8	ENE					
13 Jun 2022	7:00 AM	0.9	NE	14 Jun 2022	1:00 PM	1.8	ENE					
13 Jun 2022	8:00 AM	1.8	ENE	14 Jun 2022	2:00 PM	1.8	NE					
13 Jun 2022	9:00 AM	1.8	ENE	14 Jun 2022	3:00 PM	1.3	NE					
13 Jun 2022	10:00 AM	0.9	SW	14 Jun 2022	4:00 PM	1.8	NNE					
13 Jun 2022	11:00 AM	1.3	ENE	14 Jun 2022	5:00 PM	1.3	N					
13 Jun 2022	12:00 PM	1.3	ENE	14 Jun 2022	6:00 PM	1.3	NNE					
13 Jun 2022	1:00 PM	0.9	ENE	14 Jun 2022	7:00 PM	1.3	NNE					
13 Jun 2022	2:00 PM	1.3	SW	14 Jun 2022	8:00 PM	0.9	NNE					
13 Jun 2022	3:00 PM	1.8	ENE	14 Jun 2022	9:00 PM	1.8	NNE					
13 Jun 2022	4:00 PM	3.6	ENE	14 Jun 2022	10:00 PM	1.3	NNE					
13 Jun 2022	5:00 PM	3.1	ENE	14 Jun 2022	11:00 PM	1.8	NNE					
13 Jun 2022	6:00 PM	3.1	ENE	15 Jun 2022	12:00 AM	0.9	NNE					
13 Jun 2022	7:00 PM	2.7	ENE	15 Jun 2022	1:00 AM	1.3	N					
13 Jun 2022	8:00 PM	1.3	ENE	15 Jun 2022	2:00 AM	0.9	NNE					
13 Jun 2022	9:00 PM	1.3	ENE	15 Jun 2022	3:00 AM	0.9	NNE					
13 Jun 2022	10:00 PM	0.9	ENE	15 Jun 2022	4:00 AM	0.9	NE					
13 Jun 2022	11:00 PM	1.3	ENE	15 Jun 2022	5:00 AM	0.9	ENE					
14 Jun 2022	12:00 AM	1.3	ENE	15 Jun 2022	6:00 AM	0.4	NE					
14 Jun 2022	1:00 AM	0.9	NNE	15 Jun 2022	7:00 AM	0.0	NE					
14 Jun 2022	2:00 AM	0.4	SW	15 Jun 2022	8:00 AM	0.9	SSW					
14 Jun 2022	3:00 AM	1.3	SW	15 Jun 2022	9:00 AM	0.9	SSW					
14 Jun 2022	4:00 AM	1.3	SW	15 Jun 2022	10:00 AM	1.3	S					
14 Jun 2022	5:00 AM	0.9	SW	15 Jun 2022	11:00 AM	0.9	ENE					
14 Jun 2022	6:00 AM	0.4	Е	15 Jun 2022	12:00 PM	0.9	ENE					
14 Jun 2022	7:00 AM	0.9	SW	15 Jun 2022	1:00 PM	3.6	ENE					
14 Jun 2022	8:00 AM	0.4	ENE	15 Jun 2022	2:00 PM	2.2	ENE					
14 Jun 2022	9:00 AM	0.9	SW	15 Jun 2022	3:00 PM	1.3	ENE					
14 Jun 2022	10:00 AM	1.3	ENE	15 Jun 2022	4:00 PM	2.2	SW					
14 Jun 2022	11:00 AM	2.2	ENE	15 Jun 2022	5:00 PM	1.8	SW					

	June	2022		June 2022								
	Wind Speed a	nd Directions			Wind Speed a	and Directions						
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction					
15 Jun 2022	6:00 PM	2.2	SW	17 Jun 2022	12:00 AM	1.8	SW					
15 Jun 2022	7:00 PM	2.7	SW	17 Jun 2022	1:00 AM	0.9	SW					
15 Jun 2022	8:00 PM	1.8	SW	17 Jun 2022	2:00 AM	0.0	SW					
15 Jun 2022	9:00 PM	0.9	SSW	17 Jun 2022	3:00 AM	1.3	SW					
15 Jun 2022	10:00 PM	0.9	SSW	17 Jun 2022	4:00 AM	1.8	SW					
15 Jun 2022	11:00 PM	1.3	SW	17 Jun 2022	5:00 AM	0.4	SW					
16 Jun 2022	12:00 AM	1.3	SW	17 Jun 2022	6:00 AM	0.9	SW					
16 Jun 2022	1:00 AM	0.9	SW	17 Jun 2022	7:00 AM	1.3	SW					
16 Jun 2022	2:00 AM	0.9	SW	17 Jun 2022	8:00 AM	0.9	SW					
16 Jun 2022	3:00 AM	1.3	SW	17 Jun 2022	9:00 AM	0.9	SW					
16 Jun 2022	4:00 AM	0.4	WSW	17 Jun 2022	10:00 AM	0.9	SW					
16 Jun 2022	5:00 AM	0.9	ENE	17 Jun 2022	11:00 AM	1.3	SW					
16 Jun 2022	6:00 AM	0.4	SSE	17 Jun 2022	12:00 PM	1.3	SW					
16 Jun 2022	7:00 AM	0.9	ENE	17 Jun 2022	1:00 PM	2.2	SW					
16 Jun 2022	8:00 AM	0.4	ENE	17 Jun 2022	2:00 PM	1.3	SW					
16 Jun 2022	9:00 AM	0.9	ENE	17 Jun 2022	3:00 PM	0.9	NE					
16 Jun 2022	10:00 AM	0.9	ENE	17 Jun 2022	4:00 PM	0.4	SW					
16 Jun 2022	11:00 AM	0.9	ENE	17 Jun 2022	5:00 PM	1.3	SW					
16 Jun 2022	12:00 PM	0.9	ENE	17 Jun 2022	6:00 PM	1.3	SW					
16 Jun 2022	1:00 PM	0.9	ENE	17 Jun 2022	7:00 PM	1.3	SW					
16 Jun 2022	2:00 PM	1.8	ENE	17 Jun 2022	8:00 PM	0.4	NNE					
16 Jun 2022	3:00 PM	1.8	ENE	17 Jun 2022	9:00 PM	0.4	NNE					
16 Jun 2022	4:00 PM	0.9	ENE	17 Jun 2022	10:00 PM	0.4	SW					
16 Jun 2022	5:00 PM	2.2	SW	17 Jun 2022	11:00 PM	0.9	SW					
16 Jun 2022	6:00 PM	3.6	SW	18 Jun 2022	12:00 AM	0.4	SW					
16 Jun 2022	7:00 PM	1.3	SW	18 Jun 2022	1:00 AM	0.9	SW					
16 Jun 2022	8:00 PM	0.9	SW	18 Jun 2022	2:00 AM	0.9	SW					
16 Jun 2022	9:00 PM	0.4	SW	18 Jun 2022	3:00 AM	0.9	SW					
16 Jun 2022	10:00 PM	0.4	SW	18 Jun 2022	4:00 AM	0.4	SSW					
16 Jun 2022	11:00 PM	0.4	SW	18 Jun 2022	5:00 AM	0.4	SW					

	June	2022		June 2022								
	Wind Speed a	and Directions			Wind Speed a	and Directions						
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction					
18 Jun 2022	6:00 AM	0.9	SW	19 Jun 2022	12:00 PM	0.9	ENE					
18 Jun 2022	7:00 AM	0.9	Е	19 Jun 2022	1:00 PM	1.8	SW					
18 Jun 2022	8:00 AM	0.4	SW	19 Jun 2022	2:00 PM	2.2	SW					
18 Jun 2022	9:00 AM	0.9	SW	19 Jun 2022	3:00 PM	2.2	SW					
18 Jun 2022	10:00 AM	1.3	SW	19 Jun 2022	4:00 PM	2.2	SW					
18 Jun 2022	11:00 AM	0.9	SW	19 Jun 2022	5:00 PM	1.8	SW					
18 Jun 2022	12:00 PM	1.3	SW	19 Jun 2022	6:00 PM	1.8	SW					
18 Jun 2022	1:00 PM	1.8	SW	19 Jun 2022	7:00 PM	0.9	SW					
18 Jun 2022	2:00 PM	0.9	ENE	19 Jun 2022	8:00 PM	1.3	SW					
18 Jun 2022	3:00 PM	0.4	ENE	19 Jun 2022	9:00 PM	1.8	SW					
18 Jun 2022	4:00 PM	0.4	SW	19 Jun 2022	10:00 PM	0.9	SW					
18 Jun 2022	5:00 PM	0.9	SW	19 Jun 2022	11:00 PM	0.9	SW					
18 Jun 2022	6:00 PM	1.3	ENE	20 Jun 2022	12:00 AM	0.4	NNE					
18 Jun 2022	7:00 PM	0.4	ENE	20 Jun 2022	1:00 AM	0.0	ENE					
18 Jun 2022	8:00 PM	1.3	ENE	20 Jun 2022	2:00 AM	0.4	NE					
18 Jun 2022	9:00 PM	0.9	SW	20 Jun 2022	3:00 AM	0.4	NE					
18 Jun 2022	10:00 PM	0.4	SW	20 Jun 2022	4:00 AM	0.4	NNE					
18 Jun 2022	11:00 PM	0.4	SW	20 Jun 2022	5:00 AM	0.9	N					
19 Jun 2022	12:00 AM	0.4	SW	20 Jun 2022	6:00 AM	1.3	NNE					
19 Jun 2022	1:00 AM	0.9	SW	20 Jun 2022	7:00 AM	0.9	NNE					
19 Jun 2022	2:00 AM	0.0	SW	20 Jun 2022	8:00 AM	1.3	NNE					
19 Jun 2022	3:00 AM	0.3	ENE	20 Jun 2022	9:00 AM	0.9	NNE					
19 Jun 2022	4:00 AM	0.8	ENE	20 Jun 2022	10:00 AM	1.3	NNE					
19 Jun 2022	5:00 AM	0.2	ENE	20 Jun 2022	11:00 AM	1.3	NNE					
19 Jun 2022	6:00 AM	0.0	NE	20 Jun 2022	12:00 PM	0.9	NNE					
19 Jun 2022	7:00 AM	0.9	ENE	20 Jun 2022	1:00 PM	1.3	N					
19 Jun 2022	8:00 AM	0.4	NNE	20 Jun 2022	2:00 PM	1.8	NNE					
19 Jun 2022	9:00 AM	0.9	SW	20 Jun 2022	3:00 PM	2.2	NNE					
19 Jun 2022	10:00 AM	1.3	SW	20 Jun 2022	4:00 PM	3.1	NE					
19 Jun 2022	11:00 AM	0.4	NNE	20 Jun 2022	5:00 PM	3.1	ENE					

	June	2022		June 2022							
	Wind Speed a	nd Directions			Wind Speed a	and Directions					
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction				
20 Jun 2022	6:00 PM	3.1	NE	22 Jun 2022	12:00 AM	1.8	ENE				
20 Jun 2022	7:00 PM	2.7	ENE	22 Jun 2022	1:00 AM	1.3	ENE				
20 Jun 2022	8:00 PM	0.9	ENE	22 Jun 2022	2:00 AM	0.9	ENE				
20 Jun 2022	9:00 PM	1.8	SW	22 Jun 2022	3:00 AM	0.9	ENE				
20 Jun 2022	10:00 PM	0.9	ENE	22 Jun 2022	4:00 AM	0.9	ENE				
20 Jun 2022	11:00 PM	0.4	NNE	22 Jun 2022	5:00 AM	0.9	ENE				
21 Jun 2022	12:00 AM	0.4	ENE	22 Jun 2022	6:00 AM	0.4	ENE				
21 Jun 2022	1:00 AM	0.4	ENE	22 Jun 2022	7:00 AM	0.9	ENE				
21 Jun 2022	2:00 AM	0.4	ENE	22 Jun 2022	8:00 AM	0.9	ENE				
21 Jun 2022	3:00 AM	0.4	SE	22 Jun 2022	9:00 AM	2.2	ENE				
21 Jun 2022	4:00 AM	0.9	ENE	22 Jun 2022	10:00 AM	3.1	ENE				
21 Jun 2022	5:00 AM	1.3	ENE	22 Jun 2022	11:00 AM	1.3	NE				
21 Jun 2022	6:00 AM	1.3	ENE	22 Jun 2022	12:00 PM	2.7	ENE				
21 Jun 2022	7:00 AM	0.9	ENE	22 Jun 2022	1:00 PM	3.1	ENE				
21 Jun 2022	8:00 AM	1.3	ENE	22 Jun 2022	2:00 PM	3.1	ENE				
21 Jun 2022	9:00 AM	1.3	ENE	22 Jun 2022	3:00 PM	2.7	ENE				
21 Jun 2022	10:00 AM	1.8	ENE	22 Jun 2022	4:00 PM	2.2	ENE				
21 Jun 2022	11:00 AM	2.2	ENE	22 Jun 2022	5:00 PM	2.7	ENE				
21 Jun 2022	12:00 PM	3.1	ENE	22 Jun 2022	6:00 PM	1.8	ENE				
21 Jun 2022	1:00 PM	2.7	ENE	22 Jun 2022	7:00 PM	1.8	ENE				
21 Jun 2022	2:00 PM	3.1	ENE	22 Jun 2022	8:00 PM	2.2	ENE				
21 Jun 2022	3:00 PM	4.5	ENE	22 Jun 2022	9:00 PM	1.3	ENE				
21 Jun 2022	4:00 PM	4.0	ENE	22 Jun 2022	10:00 PM	1.3	ENE				
21 Jun 2022	5:00 PM	4.0	ENE	22 Jun 2022	11:00 PM	1.3	ENE				
21 Jun 2022	6:00 PM	4.0	ENE	23 Jun 2022	12:00 AM	1.3	ENE				
21 Jun 2022	7:00 PM	2.7	ENE	23 Jun 2022	1:00 AM	0.9	NE				
21 Jun 2022	8:00 PM	2.7	ENE	23 Jun 2022	2:00 AM	0.9	ENE				
21 Jun 2022	9:00 PM	2.7	ENE	23 Jun 2022	3:00 AM	0.9	ENE				
21 Jun 2022	10:00 PM	1.8	ENE	23 Jun 2022	4:00 AM	0.9	ENE				
21 Jun 2022	11:00 PM	1.3	ENE	23 Jun 2022	5:00 AM	0.4	ENE				

	June	2022		June 2022								
	Wind Speed a	and Directions		Wind Speed and Directions								
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction					
23 Jun 2022	6:00 AM	0.4	NNE	24 Jun 2022	12:00 PM	2.7	ENE					
23 Jun 2022	7:00 AM	0.4	NE	24 Jun 2022	1:00 PM	3.1	NE					
23 Jun 2022	8:00 AM	1.3	ENE	24 Jun 2022	2:00 PM	2.2	SW					
23 Jun 2022	9:00 AM	1.3	NE	24 Jun 2022	3:00 PM	2.7	SW					
23 Jun 2022	10:00 AM	0.9	NNE	24 Jun 2022	4:00 PM	2.2	SW					
23 Jun 2022	11:00 AM	1.3	ENE	24 Jun 2022	5:00 PM	2.2	SW					
23 Jun 2022	12:00 PM	0.9	SW	24 Jun 2022	6:00 PM	2.7	SW					
23 Jun 2022	1:00 PM	0.9	ENE	24 Jun 2022	7:00 PM	0.9	SW					
23 Jun 2022	2:00 PM	1.3	ENE	24 Jun 2022	8:00 PM	1.3	ENE					
23 Jun 2022	3:00 PM	1.3	ESE	24 Jun 2022	9:00 PM	1.3	ENE					
23 Jun 2022	4:00 PM	1.3	Е	24 Jun 2022	10:00 PM	0.9	ENE					
23 Jun 2022	5:00 PM	0.9	Е	24 Jun 2022	11:00 PM	0.9	SW					
23 Jun 2022	6:00 PM	1.3	SW	25 Jun 2022	12:00 AM	1.8	SW					
23 Jun 2022	7:00 PM	0.9	SW	25 Jun 2022	1:00 AM	0.9	SW					
23 Jun 2022	8:00 PM	0.9	Е	25 Jun 2022	2:00 AM	0.9	SW					
23 Jun 2022	9:00 PM	0.4	NE	25 Jun 2022	3:00 AM	0.9	SW					
23 Jun 2022	10:00 PM	1.3	NE	25 Jun 2022	4:00 AM	0.9	SW					
23 Jun 2022	11:00 PM	1.8	NNE	25 Jun 2022	5:00 AM	0.9	SW					
24 Jun 2022	12:00 AM	0.9	N	25 Jun 2022	6:00 AM	0.9	SW					
24 Jun 2022	1:00 AM	0.9	NNE	25 Jun 2022	7:00 AM	1.8	SW					
24 Jun 2022	2:00 AM	0.9	NNE	25 Jun 2022	8:00 AM	1.8	SW					
24 Jun 2022	3:00 AM	0.4	NNE	25 Jun 2022	9:00 AM	1.8	SW					
24 Jun 2022	4:00 AM	0.4	NNE	25 Jun 2022	10:00 AM	2.2	SW					
24 Jun 2022	5:00 AM	0.9	NNE	25 Jun 2022	11:00 AM	0.9	ESE					
24 Jun 2022	6:00 AM	1.3	NNE	25 Jun 2022	12:00 PM	1.3	ESE					
24 Jun 2022	7:00 AM	1.3	NNE	25 Jun 2022	1:00 PM	1.3	ESE					
24 Jun 2022	8:00 AM	1.3	N	25 Jun 2022	2:00 PM	1.8	SW					
24 Jun 2022	9:00 AM	0.9	NNE	25 Jun 2022	3:00 PM	2.2	SW					
24 Jun 2022	10:00 AM	1.3	NNE	25 Jun 2022	4:00 PM	2.7	SW					
24 Jun 2022	11:00 AM	3.1	NE	25 Jun 2022	5:00 PM	2.7	SW					

	June	2022		June 2022							
	Wind Speed a	nd Directions			Wind Speed a	and Directions					
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction				
25 Jun 2022	6:00 PM	3.1	NE	27 Jun 2022	12:00 AM	1.3	NNE				
25 Jun 2022	7:00 PM	2.7	NE	27 Jun 2022	1:00 AM	1.3	NNE				
25 Jun 2022	8:00 PM	0.9	NNE	27 Jun 2022	2:00 AM	1.8	NNE				
25 Jun 2022	9:00 PM	0.9	N	27 Jun 2022	3:00 AM	1.8	NNE				
25 Jun 2022	10:00 PM	1.3	NNE	27 Jun 2022	4:00 AM	1.3	NNE				
25 Jun 2022	11:00 PM	0.9	NNE	27 Jun 2022	5:00 AM	1.8	NE				
26 Jun 2022	12:00 AM	1.3	NNE	27 Jun 2022	6:00 AM	1.8	NNE				
26 Jun 2022	1:00 AM	0.4	NNE	27 Jun 2022	7:00 AM	1.8	NNE				
26 Jun 2022	2:00 AM	0.9	NNE	27 Jun 2022	8:00 AM	2.2	NNE				
26 Jun 2022	3:00 AM	0.9	NNE	27 Jun 2022	9:00 AM	2.2	NNE				
26 Jun 2022	4:00 AM	0.4	NNE	27 Jun 2022	10:00 AM	2.2	NNE				
26 Jun 2022	5:00 AM	1.3	N	27 Jun 2022	11:00 AM	1.8	NNE				
26 Jun 2022	6:00 AM	0.9	NNE	27 Jun 2022	12:00 PM	2.2	NNE				
26 Jun 2022	7:00 AM	0.9	NNE	27 Jun 2022	1:00 PM	1.8	NE				
26 Jun 2022	8:00 AM	1.3	NE	27 Jun 2022	2:00 PM	1.8	NNE				
26 Jun 2022	9:00 AM	2.2	ENE	27 Jun 2022	3:00 PM	2.2	NNE				
26 Jun 2022	10:00 AM	0.4	NE	27 Jun 2022	4:00 PM	2.2	NNE				
26 Jun 2022	11:00 AM	0.4	NE	27 Jun 2022	5:00 PM	2.7	NNE				
26 Jun 2022	12:00 PM	0.4	ENE	27 Jun 2022	6:00 PM	2.7	NE				
26 Jun 2022	1:00 PM	0.9	ENE	27 Jun 2022	7:00 PM	2.7	NE				
26 Jun 2022	2:00 PM	1.8	ENE	27 Jun 2022	8:00 PM	2.2	NNE				
26 Jun 2022	3:00 PM	0.9	SW	27 Jun 2022	9:00 PM	2.7	NNE				
26 Jun 2022	4:00 PM	0.4	Е	27 Jun 2022	10:00 PM	2.7	NNE				
26 Jun 2022	5:00 PM	0.9	ENE	27 Jun 2022	11:00 PM	2.2	NNE				
26 Jun 2022	6:00 PM	2.7	ENE	28 Jun 2022	12:00 AM	1.8	NE				
26 Jun 2022	7:00 PM	1.3	ENE	28 Jun 2022	1:00 AM	1.3	NNE				
26 Jun 2022	8:00 PM	1.3	ENE	28 Jun 2022	2:00 AM	1.8	NNE				
26 Jun 2022	9:00 PM	0.9	ENE	28 Jun 2022	3:00 AM	1.3	SSE				
26 Jun 2022	10:00 PM	0.9	SSW	28 Jun 2022	4:00 AM	2.2	NNE				
26 Jun 2022	11:00 PM	1.3	NNE	28 Jun 2022	5:00 AM	2.2	NNE				

	June	2022		June 2022								
	Wind Speed a	nd Directions			Wind Speed a	and Directions						
Date	Time	Wind Speed m-s	Direction	Date	Time	Wind Speed m-s	Direction					
28 Jun 2022	6:00 AM	2.2	NNE	29 Jun 2022	12:00 PM	2.2	WNW					
28 Jun 2022	7:00 AM	2.2	NNE	29 Jun 2022	1:00 PM	0.0						
28 Jun 2022	8:00 AM	1.8	NE	29 Jun 2022	2:00 PM	1.8	ENE					
28 Jun 2022	9:00 AM	1.8	SSW	29 Jun 2022	3:00 PM	1.8	NE					
28 Jun 2022	10:00 AM	2.7	NNE	29 Jun 2022	4:00 PM	2.2	NE					
28 Jun 2022	11:00 AM	2.2	SW	29 Jun 2022	5:00 PM	2.2	NE					
28 Jun 2022	12:00 PM	2.2	W	29 Jun 2022	6:00 PM	2.7	NNE					
28 Jun 2022	1:00 PM	2.7	W	29 Jun 2022	7:00 PM	2.7	N					
28 Jun 2022	2:00 PM	3.1	W	29 Jun 2022	8:00 PM	2.7	NNE					
28 Jun 2022	3:00 PM	3.1	W	29 Jun 2022	9:00 PM	2.2	NNE					
28 Jun 2022	4:00 PM	3.6	W	29 Jun 2022	10:00 PM	2.7	NNE					
28 Jun 2022	5:00 PM	2.2	WNW	29 Jun 2022	11:00 PM	2.7	NNE					
28 Jun 2022	6:00 PM	3.1	W	30 Jun 2022	12:00 AM	2.2	NNE					
28 Jun 2022	7:00 PM	2.7	W	30 Jun 2022	1:00 AM	1.8	NNE					
28 Jun 2022	8:00 PM	2.7	W	30 Jun 2022	2:00 AM	1.3	NNE					
28 Jun 2022	9:00 PM	2.2	W	30 Jun 2022	3:00 AM	1.8	N					
28 Jun 2022	10:00 PM	2.7	WNW	30 Jun 2022	4:00 AM	1.3	NNE					
28 Jun 2022	11:00 PM	2.2	W	30 Jun 2022	5:00 AM	2.2	NNE					
29 Jun 2022	12:00 AM	2.2	W	30 Jun 2022	6:00 AM	2.2	NE					
29 Jun 2022	1:00 AM	1.8	W	30 Jun 2022	7:00 AM	2.2	ENE					
29 Jun 2022	2:00 AM	1.8	WNW	30 Jun 2022	8:00 AM	2.2	NE					
29 Jun 2022	3:00 AM	2.2	W	30 Jun 2022	9:00 AM	1.8	NNE					
29 Jun 2022	4:00 AM	2.7	WNW	30 Jun 2022	10:00 AM	1.8	NNE					
29 Jun 2022	5:00 AM	2.2	W	30 Jun 2022	11:00 AM	2.7	NE					
29 Jun 2022	6:00 AM	2.7	W	30 Jun 2022	12:00 PM	2.2	WNW					
29 Jun 2022	7:00 AM	2.7	W	30 Jun 2022	1:00 PM	2.2	NE					
29 Jun 2022	8:00 AM	3.6	NW	30 Jun 2022	2:00 PM	0.4	NE					
29 Jun 2022	9:00 AM	2.2	WNW	30 Jun 2022	3:00 PM	0.9	NE					
29 Jun 2022	10:00 AM	2.2	W	30 Jun 2022	4:00 PM	0.4	NE					
29 Jun 2022	11:00 AM	2.7	W	30 Jun 2022	5:00 PM	0.4	NNE					

Appendix D - Weather Conditions

	June 2022													
Wind Speed and Directions														
Date														
30 Jun 2022	6:00 PM	0.4	NNE											
30 Jun 2022	7:00 PM	0.4	NNE											
30 Jun 2022	8:00 PM	0.4	NE											
30 Jun 2022	9:00 PM	0.0	ENE											
30 Jun 2022	10:00 PM	0.4	NNE											
30 Jun 2022	30 Jun 2022 11:00 PM 0.0 ENE													

June 2022										
Wind Speed and Directions										
Date Time Wind Speed m-s Direction										

APPENDIX F 24-HOUR TSP MONITORING RESULTS AND GRAPHICAL PRESENTATIONS

Appendix F - 24-hour TSP Impact Monitoring Results

Location CKL1 - Flat 121 Cha Kwo Ling Village

	Weather	Air Temp.	Atmospheric	Filter W	eight (g)	Particulate		e Time	C!	Flow Rate	e (m³/min.)	Av. Flow	Total vol.	Conc.	Action	Limit
Start Date	Condition	(K)	Pressure, Pa (mmHg)	Initial	Final	weight (g)	Initial	Final	Sampling Time (hrs.)	Initial	Final	(m³/min)		(µg/m³)	Level (µ g/m3)	Level (µ g/m3)
4-Jun-22	Cloudy	302.6	754.9	3.2850	3.4336	0.1486	4370.9	4394.9	24.0	1.21	1.21	1.21	1736.9	85.6		
9-Jun-22	Cloudy	299.2	755.1	3.3436	3.4037	0.0602	4394.9	4418.9	24.0	1.21	1.21	1.21	1744.5	34.5		
14-Jun-22	Cloudy	300.1	757.1	3.3436	3.4181	0.0745	4418.9	4443.0	24.1	1.21	1.21	1.21	1749.4	42.6	191.0	260.0
20-Jun-22	Cloudy	302.3	755.0	3.3454	3.4838	0.1384	4443.0	4467.0	24.0	1.21	1.21	1.21	1738.3	79.6	191.0	200.0
25-Jun-22	Fine	302.8	757.4	3.3826	3.4790	0.0964	4467.0	4491.0	24.0	1.21	1.21	1.21	1738.6	55.5		
29-Jun-22	Fine	301.9	753.1	3.2883	3.3787	0.0904	4491.0	4515.0	24.0	1.20	1.21	1.21	1736.9	52.0		
Note:	Bold Italic means Action Level exceedance											Min	34.5			
	Rold Italia with una	derline moone l	imit Loval avacadance										May	95.6		

Location CKL2 - Flat 103 Cha Kwo Ling Village

	\/\4b	Weather Air Temp.	emp. Atmospheric	Filter W	eight (g)	Particulate	Elaps	e Time	C!:	Flow Rate	e (m³/min.)	Av Elow	Total vol.	Conc.	Action	Limit
Start Date	Condition		Pressure, Pa (mmHg)	Initial	Final	weight (g)	Initial	Final	Sampling Time (hrs.)	Initial	Final	(m³/min)	(m ³)	(μg/m ³)	Level (µ g/m3)	Level (µ g/m3)
4-Jun-22	Cloudy	302.6	754.9	3.3042	3.4574	0.1532	16527.7	16551.7	24.0	1.21	1.21	1.21	1736.3	88.2		
9-Jun-22	Cloudy	299.2	755.1	3.3608	3.4794	0.1186	16551.7	16575.7	24.0	1.21	1.21	1.21	1745.0	68.0		
14-Jun-22	Cloudy	300.1	757.1	3.3528	3.4323	0.0796	16599.7	16623.7	24.0	1.21	1.21	1.21	1744.9	45.6	183.0	260.0
20-Jun-22	Cloudy	302.3	755.0	3.3277	3.4613	0.1336	16647.7	16671.7	24.0	1.21	1.21	1.21	1737.9	76.9	103.0	200.0
25-Jun-22	Fine	302.8	757.4	3.3808	3.5269	0.1461	16671.7	16695.7	24.0	1.21	1.21	1.21	1738.3	84.0		
29-Jun-22	Fine	301.9	753.1	3.2802	3.3982	0.1180	16695.7	16719.7	24.0	1.20	1.21	1.21	1736.3	67.9	1	
Note:	Bold Italic means A	ction Level exce	edance										Min	45.6		
	Bold Italic with und	lerline means L	imit Level exceedance										Max	88.2		
													Average	71.8		

Location KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)


	Weather	Air Temp.	Atmospheric	Filter W	eight (g)	Particulate	Elaps	e Time	Sampling	Flow Rate	e (m³/min.)	Av. Flow	Total vol.	Conc.	Action	Limit
Start Date	Condition	(K)	Pressure, Pa (mmHg)	Initial	Final	weight (g)	Initial	Final	Time (hrs.)	Initial	Final	(m³/min)		(µg/m ³)	Level (µ g/m3)	Level (µ g/m3)
4-Jun-22	Cloudy	302.6	754.9	3.3363	3.4046	0.0683	15850.9	15874.9	24.0	1.21	1.21	1.21	1741.5	39.2		
9-Jun-22	Rainy	299.2	755.1	3.3597	3.3964	0.0367	15874.9	15898.9	24.0	1.21	1.22	1.22	1749.8	21.0		
14-Jun-22	Fine	300.1	757.1	3.3717	3.4177	0.0460	15898.9	15922.9	24.0	1.21	1.22	1.22	1749.6	26.3	177.0	260.0
20-Jun-22	Cloudy	302.3	755.0	3.3681	3.4344	0.0663	15922.9	15946.9	24.0	1.21	1.21	1.21	1742.3	38.1	177.0	200.0
25-Jun-22	Sunny	302.8	757.4	3.4070	3.4530	0.0459	15946.9	15970.9	24.0	1.21	1.21	1.21	1743.4	26.3		
29-Jun-22	Fine	301.9	753.1	3.3919	3.4313	0.0394	15970.9	15994.9	24.0	1.21	1.21	1.21	1741.5	22.6		
Note:	Bold Italic means A	ction Level exce	edance										Min	21.0		
	Bold Italic with und	lerline means l	Limit Level exceedance										Max	39.2		
													Average	28.9		


Location KER1 - Future Residential Development at Kerry Godown


	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate	Elapse Time		Sampling	Flow Rate (m ³ /min.)		Av. Flow	Total vol.	Conc.	Action	Limit
Start Date				Initial	Final	weight (g)	Initial	Final	Time (hrs.)	Initial	Final		(m ³)	(μg/m ³)	Level (µ g/m3)	Level (µ g/m3)
4-Jun-22	Cloudy	302.6	754.9	3.3282	3.3764	0.0481	13499.8	13523.8	24.0	1.21	1.21	1.21	1738.3	27.7		
9-Jun-22	Rainy	299.2	755.1	3.3139	3.3602	0.0463	13523.8	13547.8	24.0	1.21	1.21	1.21	1747.3	26.5		
14-Jun-22	Sunny	300.1	757.1	3.3684	3.4173	0.0488	13547.8	13571.8	24.0	1.21	1.21	1.21	1747.1	27.9	172.0	260.0
20-Jun-22	Cloudy	302.3	755.0	3.3525	3.4537	0.1012	13583.9	13607.9	24.0	1.21	1.21	1.21	1738.5	58.2	172.0	200.0
25-Jun-22	Sunny	302.8	757.4	3.2975	3.3871	0.0896	13607.9	13631.9	24.0	1.21	1.21	1.21	1741.1	51.5		
29-Jun-22	Fine	301.9	753.1	3.3079	3.5451	0.2373	13631.9	13655.9	24.0	1.20	1.21	1.21	1738.3	136.5		
Note:	Bold Italic means A	ction Level exce	edance										Min	26.5		
	Bold Italic with und	lerline means L	imit Level exceedance										Max	136.5		
													Average	54.7		

Location KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate	Elapse Time		C!:	Flow Rate (m ³ /min.)		Av. Flow	Total vol.	Conc.	Action	Limit
				Initial	Final	weight (g)	Initial	Final	Sampling Time (hrs.)	Initial	Final	(m ³ /min)	(m ³)	(µg/m³)		Level (µ g/m3)
4-Jun-22	Cloudy	302.6	754.9	3.3411	3.3725	0.0315	14271.8	14295.8	24.0	1.21	1.21	1.21	1741.2	18.1	18.1 18.4 22.2 21.8 68.6 76.9	260.0
9-Jun-22	Rainy	299.2	755.1	3.3132	3.3453	0.0322	14295.8	14319.8	24.0	1.21	1.22	1.22	1750.5	18.4		
14-Jun-22	Fine	300.1	757.1	3.3517	3.3905	0.0389	14319.8	14343.8	24.0	1.21	1.22	1.21	1749.6	22.2		
20-Jun-22	Cloudy	302.3	755.0	3.3928	3.4309	0.0380	14343.8	14367.8	24.0	1.21	1.21	1.21	1742.0	21.8		
25-Jun-22	Sunny	302.8	757.4	3.3591	3.4786	0.1195	14367.8	14391.8	24.0	1.21	1.21	1.21	1743.1	68.6		
29-Jun-22	Fine	301.9	753.1	3.3002	3.4341	0.1339	14391.9	14415.9	24.0	1.21	1.21	1.21	1741.2	76.9		
Note: Bold Italic means Action Level exceedance												Min	18.1			
Bold Italic with underline means Limit Level exceedance												Max	76.9			
													Average	37.7		

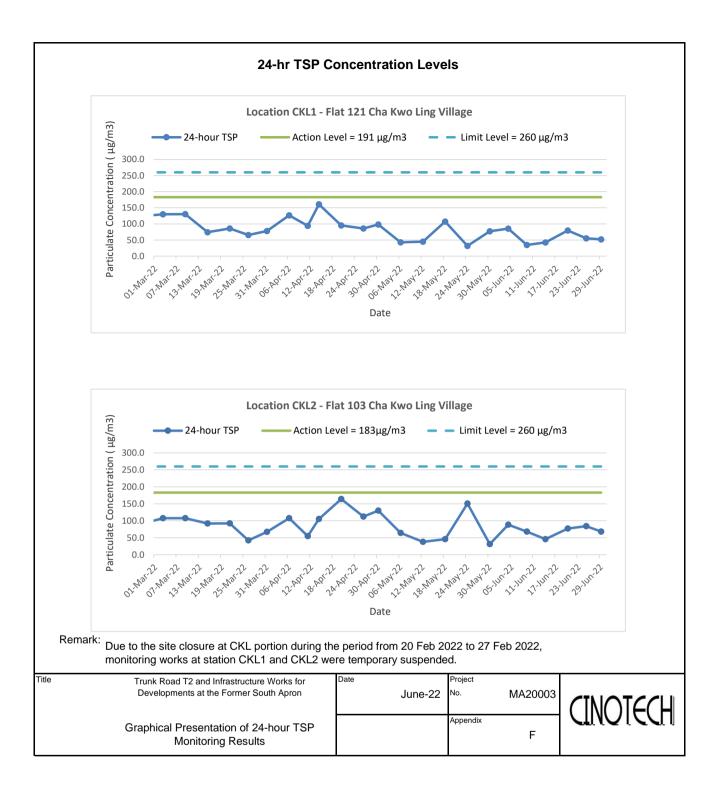

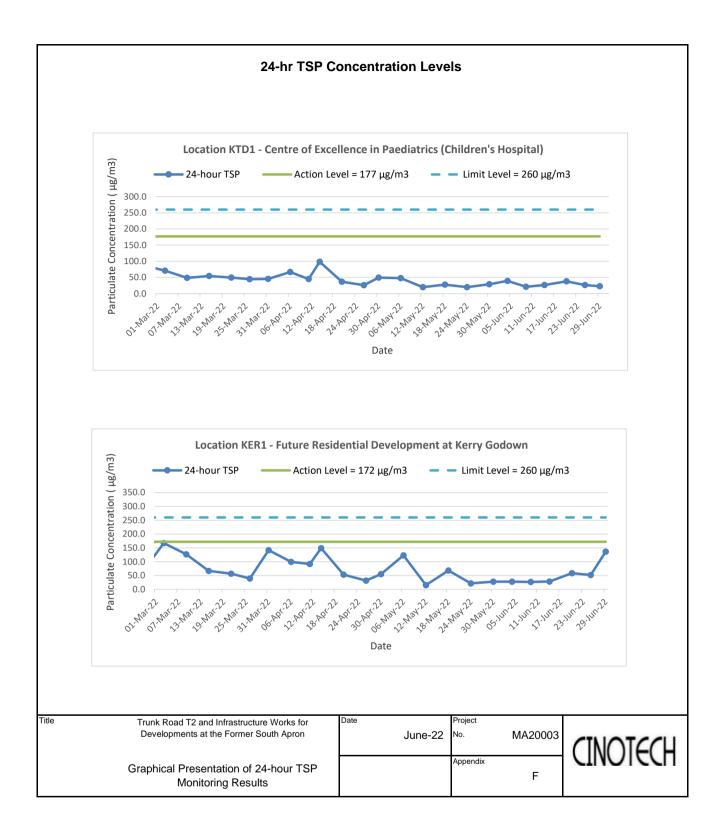

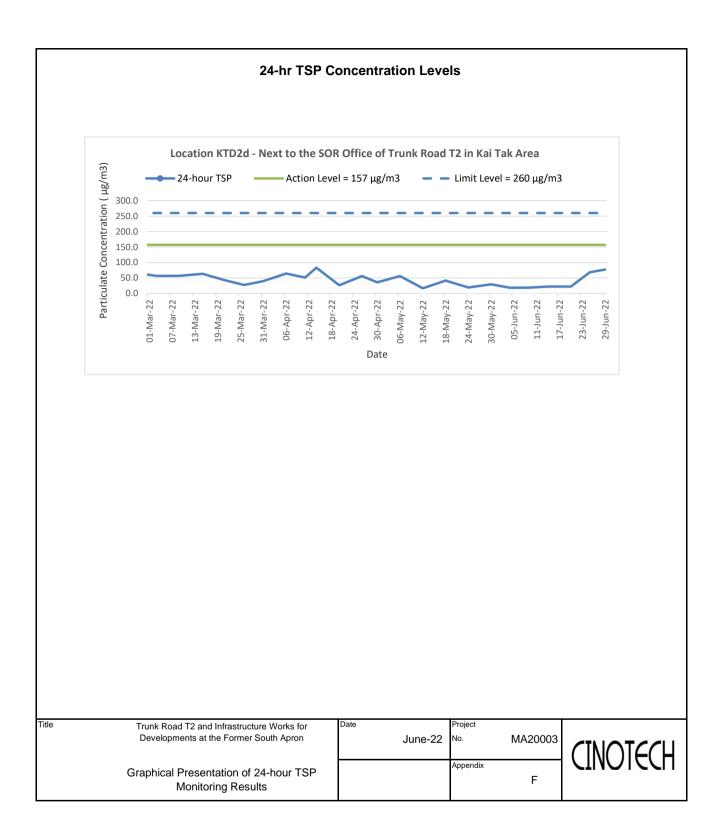

APPENDIX G COPIES OF CALIBRATION CERTIFICATES FOR NOISE MONITORING

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong Kong

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00168 Issue Date : 25 Jan 2022

Application No. : HP00044

Certificate of Calibration

Applicant : Cinotech Consultants Limited

RM 1710, Technology Park,

18 On Lai Street,

Shatin, N.T., Hong Kong

Sample Description : Submitted equipment stated to be Integrating Sound Level Meter.

Equipment No.: : N-08-11

Manufacturer: : SVANTEK

Other information :

Model No.	SVAN 957
Serial No.	23852
Microphone No.	22454

Date Received : 20 Jan 2022

Test Period : 21 Jan 2022 to 21 Jan 2022

Test Requested : Performance checking for Sound Level Meter

Test Method : The Sound Level Calibrator has been calibrated in accordance with the

documented procedures and using standard and instrument which are

recommended by the manufacturer, or equivalent.

Test conditions : Room Temperature: 22-25 degree Celsius

Relative Humidity: 35-70%

Test Result : Refer to the test result(s) on page 2.

Remark: 1. Information of the sample description provided by the Applicant.

2. The result(s) relate only to the items tested or calibrated.

For and on behalf of HIGH PRECISION CHEMICAL TESTING LIMITED

Lee Wai Kit Laboratory Manager

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong Kong

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00168 | Issue Date : 25 Jan 2022

Application No. : HP00044

Certificate of Calibration

Measuring equipment

Description	Sound Calibrator
Manufacturer	Brüel & Kjær
Model No.	TYPE 4231
Serial No.	2326353
Equipment No.	N-02-01

Test Result

Reference value, dB	Indication value, dB	Deviation, dB	Allowed deviation, dB
94.0	94.1	+0.1	± 1.5
114.0	114.2	+0.2	± 1.5

Note

- : 1. "Instrument Readings" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.
 - 2. The indication value was obtained from the average of ten replicated measurement.

- End of report -

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong Kong

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00164 Issue Date : 25 Jan 2022

Application No. : HP00042

Certificate of Calibration

Applicant : Cinotech Consultants Limited

RM 1710, Technology Park,

18 On Lai Street,

Shatin, N.T., Hong Kong

Sample Description : Submitted equipment stated to be Integrating Sound Level Meter.

Equipment No.: : N-08-12

Manufacturer: : SVANTEK

Other information

Model No.	SVAN 957
Serial No.	23851
Microphone No.	17204

Date Received : 19 Jan 2022

Test Period : 21 Jan 2022 to 21 Jan 2022

Test Requested : Performance checking for Sound Level Meter

Test Method : The Sound Level Calibrator has been calibrated in accordance with the

documented procedures and using standard and instrument which are

recommended by the manufacturer, or equivalent.

Test conditions : Room Temperature: 22-25 degree Celsius

Relative Humidity: 35-70%

Test Result : Refer to the test result(s) on page 2.

Remark: 1. Information of the sample description provided by the Applicant.

2. The result(s) relate only to the items tested or calibrated.

For and on behalf of HIGH PRECISION CHEMICAL TESTING LIMITED

Lee Wai Kit Laboratory Manager

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong Kong

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00164 | Issue Date : 25 Jan 2022

Application No. : HP00042

Certificate of Calibration

Measuring equipment

Description	Sound Calibrator
Manufacturer	Brüel & Kjær
Model No.	TYPE 4231
Serial No.	2326353
Equipment No.	N-02-01

Test Result :

Reference value, dB	Indication value, dB	Deviation, dB	Allowed deviation, dB
94.0	94.1	+0.1	± 1.5
114.0	114.2	+0.2	± 1.5

Note

- : 1. "Instrument Readings" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.
 - 2. The indication value was obtained from the average of ten replicated measurement.

- End of report -

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong Kong

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00165 Issue Date : 25 Jan 2022

Application No. : HP00043

Certificate of Calibration

Applicant : Cinotech Consultants Limited

RM 1710, Technology Park,

18 On Lai Street,

Shatin, N.T., Hong Kong

Sample Description : Submitted equipment stated to be Sound Level Calibrator.

Equipment No.: : N-09-02

Manufacturer: : SVANTEK

Other information : Mo

Model No.	SV 30A
Serial No.	10965

Date Received : 19 Jan 2022

Test Period : 21 Jan 2022 to 21 Jan 2022

Test Requested : Performance checking for Sound Level Calibrator

Test Method : The Sound Level Meter and Calibrator has been calibrated in accordance with

the documented procedures and using standard and instrument which are

recommended by the manufacturer, or equivalent.

Test conditions : Room Temperature: 22-25 degree Celsius

Relative Humidity: 35-70%

Test Result : Refer to the test result(s) on page 2.

Remark : 1. Information of the sample description provided by the Applicant.

2. The result(s) relate only to the items tested or calibrated.

For and on behalf of HIGH PRECISION CHEMICAL TESTING LIMITED

Lee Wai Kit Laboratory Manager

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong Kong

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00165 Issue Date : 25 Jan 2022

Application No. : HP00043

Certificate of Calibration

Measuring equipment

Description	Sound Calibrator
Manufacturer	Brüel & Kjær
Model No.	TYPE 4231
Serial No.	2326353
Equipment No.	N-02-01

Description	Sound Meter
Manufacturer	SVANTEK
Model No.	SVAN 957
Serial No.	21455
Microphone No.	22391
Equipment No.	N-08-07

Test Result

Reference value, dB	Indication value, dB	Deviation, dB	Allowed deviation, dB
94.0	94.0	0.0	± 0.3
114.0	114.2	+0.2	± 0.5

Note

- : 1. "Instrument Readings" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.
 - 2. The indication value was obtained from the average of ten replicated measurement.

- End of report -

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong Kong

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00171 Issue Date : 01 Apr 2022

Application No. : HP00046

Certificate of Calibration

Applicant : Cinotech Consultants Limited

RM 1710, Technology Park,

18 On Lai Street,

Shatin, N.T., Hong Kong

Sample Description : Submitted equipment stated to be Integrating Sound Level Meter.

Equipment No.: : N-12-05

Manufacturer: : BSWA Technology

Other information :

Model No.	BSWA 308
Serial No.	580287
Microphone No.	570610

Date Received : 25 Mar 2022

Test Period : 30 Mar 2022 to 30 Mar 2022

Test Requested : Performance checking for Sound Level Meter

Test Method : The Sound Level Calibrator has been calibrated in accordance with the

documented procedures and using standard and instrument which are

recommended by the manufacturer, or equivalent.

Test conditions : Room Temperature: 22-25 degree Celsius

Relative Humidity: 35-70%

Test Result : Refer to the test result(s) on page 2.

Remark: 1. Information of the sample description provided by the Applicant.

2. The result(s) relate only to the items tested or calibrated.

For and on behalf of HIGH PRECISION CHEMICAL TESTING LIMITED

Lee Wai Kit Laboratory Manager

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong Kong

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00171 Issue Date : 01 Apr 2022

Application No. : HP00046

Certificate of Calibration

Measuring equipment

Description	Sound Calibrator
Manufacturer	Brüel & Kjær
Model No.	TYPE 4231
Serial No.	2326353
Equipment No.	N-02-01

Test Result

Reference value, dB	Indication value, dB	Deviation, dB	Allowed deviation, dB
94.0	94.0	0.0	± 1.5
114.0	114.2	+0.2	± 1.5

Note

- : 1. "Instrument Readings" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.
 - 2. The indication value was obtained from the average of ten replicated measurement.

- End of report -

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong Kong

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00150 Issue Date : 16 Nov 2021

Application No. : HP00032

Certificate of Calibration

Applicant : Cinotech Consultants Limited

RM 1710, Technology Park,

18 On Lai Street,

Shatin, N.T., Hong Kong

Sample Description : Submitted equipment stated to be Sound Level Calibrator.

Equipment No.: : N-13-01

Manufacturer: : SOUNDTEK

Other information : Model No. ST-120

Serial No. 181001608

Date Received : 05 Nov 2021

Test Period : 08 Nov 2021 to 12 Nov 2021

Test Requested : Performance checking for Sound Level Calibrator

Test Method : The Sound Level Meter and Calibrator has been calibrated in accordance with

the documented procedures and using standard and instrument which are

recommended by the manufacturer, or equivalent.

Test conditions : Room Temperature: 22-25 degree Celsius

Relative Humidity: 35-70%

Test Result : Refer to the test result(s) on page 2.

Remark : 1. Information of the sample description provided by the Applicant.

2. The result(s) relate only to the items tested or calibrated.

For and on behalf of HIGH PRECISION CHEMICAL TESTING LIMITED

Lee Wai Kit Laboratory Manager

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong Kong

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00150 | Issue Date : 16 Nov 2021

Application No. : HP00032

Certificate of Calibration

Measuring equipment

Description	Sound Calibrator
Manufacturer	Brüel & Kjær
Model No.	TYPE 4231
Serial No.	2326353
Equipment No.	N-02-01

Description	Sound Meter
Manufacturer	BSWA Technology
Model No.	BSWA 308
Serial No.	570188
Microphone No.	570608
Equipment No.	N-12-03

Test Result

Reference value, dB	Indication value, dB	Deviation, dB	Allowed deviation, dB
94.0	94.1	+0.1	± 0.3
114.0	114.0	0.0	± 0.5

Note

- : 1. "Instrument Readings" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.
 - 2. The indication value was obtained from the average of ten replicated measurement.

- End of report -

APPENDIX H NOISE MONITORING RESULTS AND GRAPHICAL PRESENTATIONS

Appendix H - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)


Location CKL1 - Flat 121 Cha Kwo Ling Village									
				Unit: dE	(A) (30-min)				
Date	Time	Time Weather		Weather Measured Nois		sured Noise	Level Baseline Lev		Construction Noise Level
Date	Tillic	vvcatrici		_					
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}		
6-Jun-22	15:53	Drizzle	71.0	74.5	63.5	72.4	71 Measured ≦ Baseline		
15-Jun-22	11:41	Cloudy	73.7	76.7	63.9	72.4	68		
21-Jun-22	15:55	Cloudy	71.0 74.0 64.0 72.4		71 Measured ≤ Baseline				
27-Jun-22	15:45	Sunny	71.2	73.3	63.6	72.4	71.2 Measured ≦ Baseline		

Location CKL2 - Flat 103 Cha Kwo Ling Village								
				Unit: dB	(A) (30-min)			
Date	Time	Weather	Meas	sured Noise I	_evel	Baseline Level	Construction Noise Level	
Date	111110	vvoainor						
			L _{eq}	L ₁₀	L 90	L _{eq}	L _{eq}	
6-Jun-22	15:20	Cloudy	72.1	75.1	66.2	71.4	64	
15-Jun-22	10:58	Cloudy	70.3	0.3 73.5 61.9 71.4 70.3 Measured ≤ I		70.3 Measured ≤ Baseline		
21-Jun-22	15:20	Cloudy	72.9 75.8 66.5 71.4		68			
27-Jun-22	16:45	Sunny	70.8	73.0	58.9	71.4	70.8 Measured ≤ Baseline	

Location KTD1 - Centre of Excellence in Paediatrics (Rooftop of Children's Hospital)								
				Unit: dB (A) (30-min)				
Date	Time	Weather	Meas	Measured Noise Level			Construction Noise Level	
Date	Tillic	vvcatrici						
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	
6-Jun-22	13:03	Cloudy	70.6	72.1	68.7	78.0	70.6 Measured ≤ Baseline	
15-Jun-22	14:01	Cloudy	70.1	73.2	67.1	78.0	70.1 Measured ≦ Baseline	
21-Jun-22	13:10	Cloudy	72.0 73.2 70.2 78.0 72 Measured ≦		72 Measured ≦ Baseline			
27-Jun-22	15:47	Fine	69.5	70.8	58.4	78.0	69.5 Measured ≤ Baseline	

Location KER1 - Future Residential Development at Kerry Godown									
				Unit: dB (A) (30-min)					
Date	Time Weather		Measured Noise Level			Baseline Level	Construction Noise Level		
Date	111110	VVCatiloi		_					
			L _{eq}	L ₁₀	L 90	L _{eq}	L _{eq}		
6-Jun-22	12:11	Cloudy	61.7	62.8	60.2	65.0	61.7 Measured ≤ Baseline		
15-Jun-22	13:00	Cloudy	72.2	75.1	69.3	65.0	71		
21-Jun-22	14:25	Cloudy	66.9 67.7 65.0 65.0		62				
27-Jun-22	15:14	Sunny	67.4	68.5	64.0	65.0	64		

Location KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area									
				Unit: dB (A) (30-min)					
Date	Time	Weather	Meas	sured Noise I	_evel	Baseline Level	Construction Noise Level		
Date	Time	VVCatrici							
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}		
6-Jun-22	15:24	Cloudy	62.8	65.0	60.0	64.0	63 Measured ≦ Baseline		
15-Jun-22	15:45	Cloudy	66.2	68.1	63.0	64.0	62		
21-Jun-22	11:35	Cloudy	60.6	60.6 61.4 57.2 64.0 61 Measured ≤ Ba		61 Measured ≦ Baseline			
27-Jun-22	16:30	Fine	74.3	77.7	61.1	64.0	74		

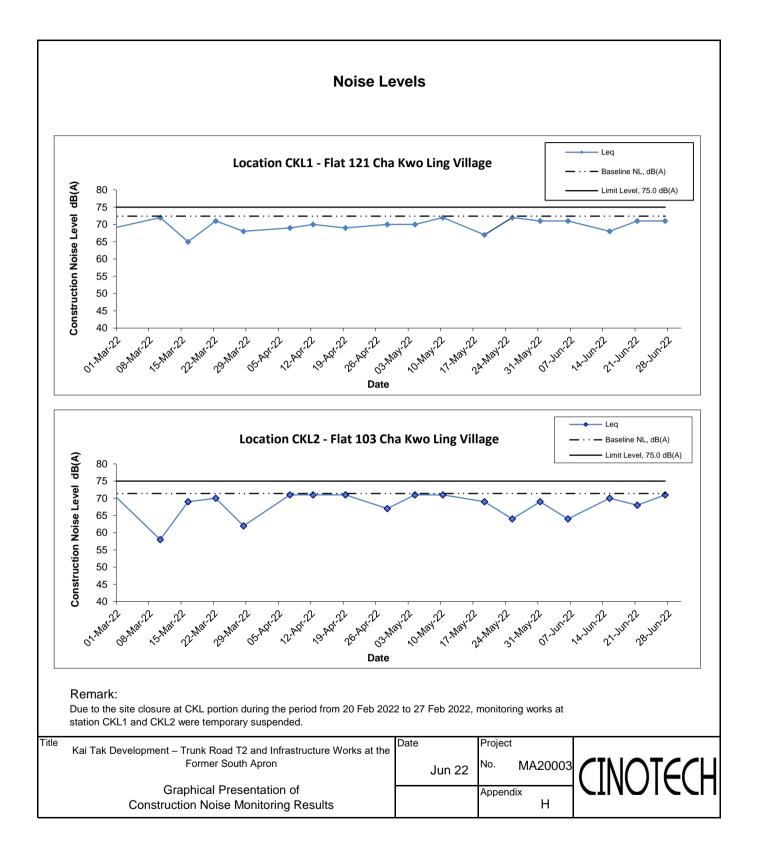

Noise Levels Location KTD1 - Centre of Excellence in Paediatrics Baseline NL. dB(A) (Children's Hospital) Construction Noise Level dB(A) 80 75 70 65 60 55 50 45 40 03.Nav.22 31.1184.72 Date Location KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area Limit Level, 75.0 dB(A) Construction Noise Level dB(A) 90 85 80 75 70 65 60 55 50 45 40 77.May 22 24,1184,22 31.May 22 07.JUN-22 Date **Location KER1 - Future Residential Development at Kerry** Baseline NL dB(A) Godown Limit Level, 75.0 dB(A) Construction Noise Level dB(A) 80 75 70 65 60 55 50 45 40 31.118472 01.7mv35 Date Project Kai Tak Development - Trunk Road T2 and Infrastructure Works at the Former South Apron MA20003 Jun 22 Graphical Presentation of Appendix Н Construction Noise Monitoring Results

APPENDIX I SITE AUDIT SUMMARY

Environmental Team for Trunk Road T2 and Infrastructure Works at the Former South Apron

Checklist Reference Number	220602
Date	02 June 2022 (Thursday)
Time	09:30 – 12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	B. Water Quality No environmental deficiency was identified during site inspection.	
220602 – R1	 C. Air Quality Stockpile of dusty material (e.eg. bags of cement and excavated mud) shall be covered by impervious sheet on top as a dust suppression measures. 	C9, C20
220602 - R2	NRMM labels shall be displayed on regulated machines.	C21
	 D. Construction Noise Impact No environmental deficiency was identified during site inspection 	
	 E. Waste/Chemical Management No environmental deficiency was identified during site inspection 	
	 F. Visual and Landscape No environmental deficiency was identified during site inspection. 	
	 G. Permits/Licences No environmental deficiency was identified during site inspection. 	
	 H. Marine Ecology No environmental deficiency was identified during site inspection. 	
	 I. Others Follow up on the previous session (Ref No.:220526), item 220526-R2 needed to be followed up on the next audit session. 	

	Name	Signature	Date
Recorded by	Tim Lui	Cyli	02 June 2022
Checked by	Karina Chan	Zalle	02 June 2022

Environmental Team for Trunk Road T2 and Infrastructure Works at the Former South Apron

Checklist Reference Number	220609
Date	09 June 2022 (Thursday)
Time	09:30 – 12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	 B. Water Quality No environmental deficiency was identified during site inspection. 	10011110
	 C. Air Quality No environmental deficiency was identified during site inspection. 	
	 D. Construction Noise Impact No environmental deficiency was identified during site inspection 	
220609 - R1	 E. Waste/Chemical Management Contractor is reminded to provide drip tray to prevent accidentally leakage of oil during chemical handling. 	E9
	 F. Visual and Landscape No environmental deficiency was identified during site inspection. 	
	 G. Permits/Licences No environmental deficiency was identified during site inspection. 	
	 H. Marine Ecology No environmental deficiency was identified during site inspection. 	
	 I. Others Follow up on the previous session (Ref No.:220602), all item has been rectified. 	

	Name	Signature	Date
Recorded by	Tim Lui	Cyli	09 June 2022
Checked by	Karina Chan	Zalle	09 June 2022

Environmental Team for Trunk Road T2 and Infrastructure Works at the Former South Apron

Checklist Reference Number	220616
Date	16 June 2022 (Thursday)
Time	09:30 – 12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	B. Water Quality	
	No environmental deficiency was identified during site inspection.	
	C. Air Quality	
	No environmental deficiency was identified during site inspection.	
	D. Construction Noise Impact	
	No environmental deficiency was identified during site inspection.	
	E. Waste/Chemical Management	
	No environmental deficiency was identified during site inspection.	
	F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	H. Marine Ecology	
	No environmental deficiency was identified during site inspection.	
	I. Others	
	• Follow up on the previous session (Ref No.:220609), all item has been rectified.	

	Name	Signature	Date
Recorded by	Tim Lui	Cyli	16 June 2022
Checked by	Karina Chan	Zalle	16 June 2022

Environmental Team for Trunk Road T2 and Infrastructure Works at the Former South Apron

Checklist Reference Number	220623
Date	23 June 2022 (Thursday)
Time	09:30 – 12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	B. Water Quality	
	No environmental deficiency was identified during site inspection.	
	C. Air Quality	
	No environmental deficiency was identified during site inspection.	
	D. Construction Noise Impact	
	No environmental deficiency was identified during site inspection.	
	E. Waste/Chemical Management	
	No environmental deficiency was identified during site inspection.	
	F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	H. Marine Ecology	
	No environmental deficiency was identified during site inspection.	
	I. Others	
	• Follow up on the previous session (Ref No.:220616), no major environmental deficiency was identified during site inspection.	

	Name	Signature	Date
Recorded by	Tim Lui	Cyli	23 June 2022
Checked by	Karina Chan	Jalle	23 June 2022

Environmental Team for Trunk Road T2 and Infrastructure Works at the Former South Apron

Checklist Reference Number	220630
Date	30 June 2022 (Thursday)
Time	09:30 – 12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	B. Water Quality	
	No environmental deficiency was identified during site inspection.	
	C. Air Quality	
	No environmental deficiency was identified during site inspection.	
	D. Construction Noise Impact	
	No environmental deficiency was identified during site inspection.	
	E. Waste/Chemical Management	
	No environmental deficiency was identified during site inspection.	
	F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	H. Marine Ecology	
	No environmental deficiency was identified during site inspection.	
	I. Others	
	• Follow up on the previous session (Ref No.:220623), no major environmental deficiency was identified during site inspection.	

	Name	Signature	Date
Recorded by	Tim Lui	Cyli	30 June 2022
Checked by	Karina Chan	Zalle	30 June 2022

APPENDIX J EVENT AND ACTION PLANS

Table J-1 Event/Action Plan for Air Construction Dust Monitoring

Table J-1	EvenuAction Figure 101 An	Constituction Dust Monitor	. mg	
Event		Ac	tion	
Event	ET	IEC	ER	Contractor
Action Level				
1. Exceedance for	1. Identify source, investigate	Check monitoring data	1. Notify Contractor.	1. Rectify any unacceptable
one sample	the causes of complaint and	submitted by ET;		practice;
	propose remedial measures;	2. Check Contractor's working		2. Amend working methods
	2. Inform IEC and ER;	method.		agreed with the ER as
	3. Repeat measurement to			appropriate.
	confirm finding;			
	4. Increase monitoring			
	frequency.			
2. Exceedance by	1. Identify source;	Check monitoring data	1. Notify Contractor;	1. Submit proposals for
two or more	2. Inform IEC and ER;	submitted by ET;	2. Ensure remedial measures	remedial actions to IEC
consecutive	3. Advise the ER on the	2. Check Contractor's working	properly implemented.	within three working days of
samples	effectiveness of the proposed	method;		notification;
	remedial measures;	3. Discuss with ET, ER and		2. Implement the agreed
	4. Repeat measurements to	Contractor on possible		proposals;
	confirm findings;	remedial measures if		3. Amend proposal if
	5. Increase monitoring	required;		appropriate.
	frequency to daily;	4. Advise the ER on the		
	6. Discuss with IEC, ER and	effectiveness of the proposed		
	Contractor on remedial	remedial measures;		
	actions required;			

E	Action			
Event	ET	IEC	ER	Contractor
Limit level 1. Exceedance for one sample	 If exceedance continues, arrange meeting with IEC, Contractor and ER; If exceedance stops, cease additional monitoring. Identify source, investigate the causes of exceedance and propose remedial measures; Inform the IEC, ER, and Contractor; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC and ER 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET, ER and Contractor on possible remedial measures; Advise the ER and ET on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Notify Contractor; Ensure remedial measures properly implemented. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to the ER and copy to the ET and IEC within three working days of notification; Implement the agreed proposals; Amend proposal if appropriate.
2. Exceedance for	informed of the results. 1. Notify IEC, ER and	1 Discuss amongst ED ET and	Confirm receipt of	Take immediate action to
	Notify IEC, ER and Contractor;	Discuss amongst ER, ET, and Contractor on the potential	notification of exceedance in	avoid further exceedance;
two or more consecutive	2. Identify source;	remedial actions;	writing;	2. Submit proposals for remedial

Errord	Action				
Event	ET	IEC ER	Contractor		
samples	3. Repeat measurement to	2. Review Contractor's 2. Notify Contractor;	actions to ER and copy to the		
	confirm findings;	remedial actions whenever 3. In consolidation with the IEC	IEC and ET within three		
	4. Increase monitoring	necessary to assure their and ET, agree with the	working days of notification;		
	frequency to daily;	effectiveness and advise the Contractor on the remedial	3. Implement the agreed		
	5. Carry out analysis of	ER and ET accordingly; measures to be implemented;	proposals;		
	Contractor's working	3. Supervise the 4. Ensure remedial measures	4. Resubmit proposals if		
	procedures with the ER to	implementation of remedial properly implemented;	problem still not under		
	determine possible mitigation	measures. 5. If exceedance continues,	control;		
	to be implemented;	consider what portion of the	5. Stop the relevant portion of		
	6. Arrange meeting with IEC	work is responsible and	works as determined by the		
	and ER to discuss the	instruct the Contractor to	ER until the exceedance is		
	remedial actions to be taken;	stop that portion of work	abated.		
	7. Assess effectiveness of	until the exceedance is			
	Contractor's remedial actions	abated.			
	and keep IEC, EPD and ER				
	informed of the results;				
	8. If exceedance stops, cease				
	additional monitoring.				

Table J-2 Event/Action Plan for Construction Noise Monitoring

TO 4	Action					
Event	ET	IEC ER	Contractor			
Action Level	1. Notify IEC, ER and	1. Review the monitoring data 1. Notify Contractor;	1. Submit noise mitigation			
	Contractor;	submitted by the ET; 2. Require Contractor to propose	proposals to the ER and copy			
	2. Carry out investigation;	2. Review the construction remedial measures for	to the IEC and ET;			
	3. Report the results of	methods and proposed redial implementation if required.	2. Implement noise mitigation			
	investigation to the IEC and	measures by the Contractor,	proposals.			
	Contractor;	and advise the ET and ER if				
	4. Discuss jointly with the ER	the proposed remedial				
	and formulate remedial	measures would be				
	measures;	sufficient.				
	5. Increase monitoring					
	frequency to check					
	mitigation effectiveness.					
Limit Level	1. Notify IEC, ER and	1. Discuss amongst ER, ET, and 1. Confirm receipt of	1. Take immediate action to			
	Contractor;	Contractor on the potential notification of failure in	avoid further exceedance;			
	2. Identify source;	remedial actions; writing;	2. Submit proposals for			
	3. Repeat measurements to	2. Review the Contractor's 2. Notify Contractor;	remedial actions to the ER			
	confirm findings;	remedial actions whenever 3. Require Contractor to	and copy to the ET and IEC			
	4. Carry out analysis of	necessary to assure their propose remedial measures	within 3 working days of			
	Contractor's working	effectiveness and advise the for the analysed noise	notification;			

E4	Action			
Event	ET	IEC	ER	Contractor
	procedures to determine	ER accordingly;	problem;	3. Implement the agreed
	possible mitigation to be	3. Supervise the	4. Ensure remedial measures	proposals;
	implemented;	implementation of remedial	properly implemented;	4. Resubmit proposals if
	5. Record the causes and action	measures.	5. If exceedance continues,	problem still not under
	taken for the exceedances;		consider what portion of the	control;
	6. Increase the monitoring		work is responsible and	5. Stop the relevant portion of
	frequency;		instruct the Contractor to stop	works as determined by the
	7. Assess the effectiveness of		that portion of work until the	ER until the exceedance is
	the Contractor's remedial		exceedance is abated.	abated.
	action with the ER and keep			
	the IEC informed of the			
	results;			
	8. If exceedance stops, cease			
	additional monitoring.			

Table J-3 Event/Action Plan for Landscape and Visual

Event	Action			
	ET	IEC	ER	Contractor
Non-conformity	1. Identify Source;	1. Check report;	1. Notify Contractor;	1. Amend working methods;
on one occasion	2. Inform the IEC and the ER;	2. Check Contractor's working	2. Ensure remedial measures	2. Rectify damage and undertake
	3. Discuss remedial actions with	method;	are properly implemented.	any necessary replacement.
	IEC, ER and Contractor	3. Discuss with ET and the		
	4. Monitor remedial actions until	Contractor on possible		
	rectification has been	remedial measures;		
	completed.	4. Advise ER on effectiveness		
		of proposed remedial		
		measures;		
		5. Check implementation of		
		remedial measures		

Event	Action		
	ET	IEC	ER Contractor
Repeated	1. Identify source;	1. Check monitoring report; 1. Notify	Contractor; 1. Amend working methods;
Non-conformity	2. Inform the IEC and the ER;	2. Check Contractor's working 2. Ensure	remedial measures 2. Rectify damage and undertake
	3. Increase monitoring frequency;	method; are pro	perly implemented. any necessary replacement.
	4. Discuss remedial actions with	3. Discuss with ET and the	
	the IEC, the ER and the	Contractor on possible	
	Contractor;	remedial measures;	
	5. Monitor remedial actions until	4. Advise ER on effectiveness	
	rectification has been	of proposed remedial	
	completed;	measures;	
	6. If exceedance stops, cease	5. Check implementation of	
	additional monitoring.	remedial measures	

APPENDIX K ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE (EMIS)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Impler	nentatio	Status	
						D	С	0	
Air Quality Impa	act			1					
S2.3.1.1	The specific mitigation comprises the following:	To minimize dust emission during	conveyor belts and	Contractor and Sub- contractors	APCO / EIAO	Y	Y		۸
	watering of the construction areas 12 times per day to reduce dust emissions by 91.7%, with reference to the "Control of Open Fugitive Dust Sources" (USEPA	construction works	stockpiles						
	AP-42). The amount of water to be applied would be $0.91 L/m^2$ for the respective watering frequency;								
	Dust enclosures with watering would be provided along the loading ramps and conveyor belts for unloading the C&D materials to the barge for dust suppression; and								N/A(1)
	3-sided barriers around the stockpiling areas WA3 and WA4.								^
S2.3.1.2	The dust control measures detailed below shall also be incorporated into the Contract Specification where practicable as an integral part of good construction practice:	To minimize dust emission during construction works	All relevant works sites	Contractor and Sub- contractors	APCO / EIAO	Y	Y		۸
	Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather;								
	Use of frequent watering for particularly dusty construction areas and areas close to ASRs;								۸
	Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines;								۸

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	С	0	
	Open stockpiles shall be avoided or covered. Prevent placing dusty material storage piles near ASRs;								əle
	Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations;								۸
	Establishment and use of vehicle wheel and body washing facilities at the exit points of the site;								۸
	Imposition of speed controls for vehicles on unpaved site roads, 8 km per hour is the recommended limit;								N/A(1)
	Routing of vehicles and position of construction plant should be at the maximum possible distance from ASRs;								۸
	Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;								*
	Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed; and								N/A(1)
	Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system.								N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	С	0	
Noise Impact		1	1				1	1	
S3.4.1.1	The use of quieter plant, including Quality Powered Mechanical Equipment (QPME) is specified for the list of equipment: - Concrete lorry mixer - Dump Truck, 5.5 tonne < gross vehicle weight ≤ 38 tonne - Generator, Super Silenced, 70 dB(A) at 7m - Poker, vibratory, Hand-held (electric) - Water Pump, Submersible (Electric) - Mobile Crane - KOBELCO CKS900 - Excavator, wheeled/tracked - HYUNDAI R80CR-9	To minimise airborne noise impacts	All relevant works sites	Contractor and Sub- contractors	NCO / EIAO		Y		۸
S3.4.1.1	Use of temporary or fixed noise barriers with a surface density of at least 10kg/m^2 to screen noise from movable and stationary plant.	To minimise air- borne noise impacts	All relevant works sites	Contractor and Sub- contractors	NCO / EIAO		Y		۸
S3.4.1.1	Use of enclosures with covers at top and three sides and a surface density of at least 10kg/m ² to screen noise from generally static noisy plant such as air compressors.	To minimise air- borne noise impacts	All relevant works sites	Contractor and Sub- contractors	NCO / EIAO		Y		N/A(1)
S3.4.1.1	Use of acoustic fabric for the silent piling system, drill rigs, rock drills etc.	To minimise air- borne noise impacts	All relevant works sites	Contractor and Sub-contractors	NCO / EIAO		Y		۸
S3.4.1.1	Proper fitting of silencers and mufflers on the ventilation fans.	To minimise air- borne noise impacts	All relevant works sites	Contractor and Sub-contractors	NCO / EIAO		Y		N/A(1)
S3.4.1.1	Implementation of good site practice: Only well-maintained plant should be operated on-site and plants should be serviced regularly during the construction period; Mobile plant, if any, should be sited as far from NSRs as possible; Plant known to emit noise strongly in one direction should, wherever possible, be properly orientated so that the noise is directed away from the nearby NSRs;	To minimise airborne noise impacts	All relevant works sites	Contractor and Sub- contractors	NCO / EIAO		Y		^

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Impler	nentatio	n Stages	Status
						D	С	0	
	Use of site hoarding as a noise barrier to screen noise at low level NSRs;								۸
	Machines and plant that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum; and								۸
	Any material stockpiles and other structures should be effectively utilised, wherever practicable, to screen the noise from on-site construction activities.								۸
	The advancing speed of the TBM should be restricted to 2m/hr in order to ensure compliance with the daytime ground-borne noise limits.								N/A
Water Quality									
S4.2.1.1	In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN 1/94), construction phase mitigation measures shall include the following: Surface run-off from the construction site, including all Works Areas, will be discharged into storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sedimentation basins. At the establishment of works sites and works areas including the barging point, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided to divert the storm water to the silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the Contractor prior to the commencement of construction and the catch-pits and perimeter channels would be constructed in advance of site formation works and earthworks;	To control water quality impact from construction site runoff and general construction activities	All works sites	Contractor and Sub- contractors	Water Pollution Control Ordinance / ProPECC PN 1/94		Y		^
	Dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas and Works Areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a site/sediment trap;								۸

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implen	nentatio	n Stages	Status
						D	С	0	
	The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/sand traps should be 5 minutes under maximum flow conditions. The sizes may vary depending upon the flow rate, but for a flow rate of 0.1m^3 /s, a sedimentation basin of 30m^3 would be required and for a flow rate of 0.5m^3 /s the basin would be 150m^3 . All effluent discharged from the construction site should comply with the standards stipulated in the TM-DSS. The detailed design of the sand/silt traps shall be undertaken by the Contractor prior to the commencement of construction;								N/A(1)
	In accordance with ProPECC PN 1/94, the construction works should be programmed to minimise surface excavation works during rainy seasons (April to September), as far as practicable. All exposed earth areas should be completed and vegetated as soon as possible after the earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means;								۸
	The overall slope of works sites should be kept to a minimum to reduce the erosive potential of surface water flows, and all trafficked areas and access roads should be protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during the prolonged periods of inclement weather and the reduction of surface sheet flows;								۸
	All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure their proper and efficient operation at all times particularly following rainstorms. Deposited silts and grits should be removed regularly and disposed of by spreading evenly over stable, vegetated areas;								۸
	Measures should be taken to minimise the ingress of site drainage into excavations. If the excavation of trenches in wet season is inevitable, they should be dug and backfilled in short sections wherever practicable. The water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities;								۸

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implem	mentatio	n Stages	Status
						D	С	0	
	Open stockpiles of construction materials (for example, aggregates, sand and fill material) should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system;								۸
	Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers;								۸
	Precautions to be taken at any time of the year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted and during or after rainstorms, are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events;								N/A(1)
	All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at the exit of every construction site where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-washing bay to public roads should be paved with sufficient backfall toward the wheel- washing bay to prevent vehicle tracking of soil and silty water to public roads and drains;								۸
	Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources, specifically Works Areas WA1, WA2, WA4 and WA5 where plant maintenance is proposed. Oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for oil interceptors to prevent flushing during heavy rain;								N/A(1)
	The construction solid waste, debris and rubbish on-site should be collected, handled and disposed of properly to avoid causing any water quality impacts. The requirements for solid waste management are detailed in Section 11 Waste Management of this EIA report; and								۸
	All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching the nearby WSRs.								*

EM&A Ref.		Objectives of the Recommended Measures & Main Concern to Address	Recommended Measures & Main	led Ag	Implementation Agent	Relevant Standard or Requirement	Impler	mentatio	n Stages	Status
						D	С	0		
S4.2.1.1 and 4.3.1.5	There is a need to apply to the EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. Minimum distances of 100m should be maintained between the discharge points of construction site effluent and the existing seawater intakes. The beneficial uses of the treated effluent for other onsite activities such as dust suppression, wheel washing and general cleaning etc, can minimise water consumption and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license	To control water quality impact from effluent discharge from construction site	All works sites	Contractor and Sub- contractors	Water Pollution Control Ordinance		Y		N/A(1)	
S4.2.1.1	Specific mitigation measures for the tunnelling works using TBM, soft ground and mechanical excavation techniques should include the following: The cut-and-cover tunnelling works should be conducted sequentially as far as practicable to limit the amount of construction wastewater generated from the exposed areas during the wet season (April to September);	To minimize construction water quality impact from tunnelling and excavation works	All tunnelling and excavation portion	Contractor and Sub- contractors	TMEIA TMwater ProPECC PN 1/94 WPCO		Y		N/A	
	Uncontaminated discharge should pass through settlement tanks prior to discharge; If contaminated groundwater is found during the course of the works, no direct discharge of groundwater from contaminated areas should be adopted. Any contaminated groundwater should be properly treated in compliance with the requirements of the TM-DSS. If wastewater treatment is to be deployed for treating the contaminated groundwater, the wastewater treatment unit should deploy suitable treatment processes (e.g. oil interceptor/activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (such as TPH) to an undetectable range;								N/A N/A	
	If groundwater recharging wells are deployed, recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in the Section 2.3 of TM-DSS;								N/A	

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Impler	nentatio	n Stages	Status
						D	С	0	
	The baseline groundwater quality shall be determined prior to the selection of the recharge wells, and submit a working plan (including the laboratory analytical results showing the quality of groundwater at the proposed recharge location(s) as well as the pollutant levels of groundwater to be recharged) to EPD for agreement. Pollution levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the recharge well. Prior to recharge, any prohibited substances such as TPH products should be removed as necessary by installing the petrol interceptor;								N/A
	The wastewater with high concentrations of SS should be treated such as by settlement in tanks with sufficient retention time before discharge. Oil interceptors would also be required to remove the oil, lubricants and grease from the wastewater.								N/A
S4.2.1.1	In order to prevent any accidental release of bentonite slurry from getting into the surrounding environment, the following specific control measures shall be followed to reduce the risk and impacts of accidental spillage: All bentonite slurry should be stored in a container that resistant to corrosion, maintained in good conditions and securely closed; The container should be labelled in English and Chinese and note that the container is for storage of bentonite slurry only; The storage container should be placed on an area of impermeable flooring and bunded with capacity to accommodate 110% of the volume of the container size	To control water quality impact from bentonite slurry	All relevant works sites	Contractor and Sub- contractors	WPCO		Y		^ N/A(1)
	or 20% by volume stored in the area and enclosed with at least 3 sides; The storage container should be sufficiently covered to prevent rainfall entering the container or bunded area (water collected within the bund must be tested and disposed of as chemical waste, if necessary); An emergency clean up kit shall be readily available where bentonite fluid will be stored or used; and								N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implen	nentatio	n Stages	Status
						D	C	0	
	The handling and disposal of bentonite slurries should be undertaken in accordance within ProPECC PN 1/94. Surplus bentonite slurries used in construction works shall be reconditioned and reused wherever practicable. Residual bentonite slurry shall be disposed of from the site as soon as possible as stipulated in Clause 8.56 of the General Specification for Civil Engineering Works. The Contractor should explore alternative disposal outlets for the residual bentonite slurry (dewatered bentonite slurry to be disposed to a public filling area and liquid bentonite slurry, if mixed with inert fill material, to be disposed to a public filling area) and disposal at landfill should be the last resort.								N/A(1)
S4.2.1.1	The proposed barging point at South Apron will not involve marine works like dredging or modifying the submerged portion of the existing seawall. As such, no direct adverse water quality impacts are anticipated during its construction or operation. However, mitigation measures as outlined above should be applied to minimise water quality impacts from site run-off and temporary open stockpiles of spoil at the proposed barging point, where appropriate. Other good site practices include: All vessels should be sized so that adequate clearance is maintained between	To minimize construction water quality impact from barging point	Barging Point	Contractor and Sub- contractors	EIAO-TM WPCO		Y		N/A(1)
	vessels and the seabed in all tide conditions, to ensure that undue turbidity is not constant by turbulance from useal movement or propaller useb. All hopper barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material;								۸
	Construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site; and								N/A(1)
	Loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water. Barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation.								N/A
S4.2.1.1		To minimize construction water quality impact from sewage and effluent	All works sites	Contractor	WPCO		Y		۸

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	mmended Agent		Relevant Standard or Requirement	Impler	nentatio	n Stages	Status
						D	С	0	
S4.2.1.1	In order to protect against impacts to the surrounding marine waters of the KTTS and Victoria Harbour in the event of an accidental spillage of fuel or oil, the Contractor will be required to prepare a spill response plan to the satisfaction of AFCD, EPD, FSD, Police, TD and WSD to define procedures for the control, containment and clean-up of any spillage that could occur on the construction site.	To control water quality impact from accidental chemical spillage	All works sites	Contractor	EIAO-TM WPCO WDO		Y		N/A(1)
S4.2.1.1	The Contractor must, also, register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	To control water quality impact from accidental chemical spillage	All works sites	Contractor	EIAO-TM WPCO WDO		Y		N/A(1)
S4.2.1.1	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	To control water quality impact from accidental chemical spillage	All works sites	Contractor	EIAO-TM WPCO WDO		Y		N/A(1)
S4.2.1.1	Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows:	To control water quality impact from accidental chemical spillage	All works sites	Contractor	EIAO-TM WPCO WDO		Y		۸
	Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport;								
	Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents; and								N/A(1)
	Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.								۸

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implem	nentatio	n Stages	Status
						D	С	0	
S4.2.1.1	The road drainage in the tunnel should pass through oil interceptors to remove oil, and grease before being discharged into the public storm water drainage system;	To mitigate runoff from tunnel during the operational phase	Tunnel	CEDD	WPCO			Y	N/A
	Silt traps and oil interceptors should be cleaned and maintained regularly; and								N/A
	The oily contents of oil interceptors should be transferred to an appropriate disposal facility, or to be collected for reuse, if possible.								N/A
Marine Ecology									
S5.3.1.1	Good construction practice measures have been recommended to be implemented as follows:	Minimize waste generation during construction	Contractor	Work Sites	Construction phase of Main Works Stage 1, Stage 2 and Stage 3		Y		N/A(1)
	Avoid damage and disturbance to the remaining and surrounding natural habitat;								
	Placement of equipment in designated areas within the existing disturbed land;								N/A(1)
	Spoil heaps should be covered at all times;								N/A(1)
	Construction activities should be restricted to the designated works areas; and								N/A(1)
	Disturbed areas to be reinstated immediately after completion of the works.								N/A(1)
Fisheries									
S6.2.1.2	No fisheries specific mitigation measures.								

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implem	nentatio	n Stages	Status
						D	С	0	
Landscape and	Visual					ı			
\$7.2.1.2	All works shall be carefully designed to minimize impacts on existing landscape resources and visually sensitive receivers. Existing trees within works area shall be retained and protected.	To minimise impact on existing trees	All relevant works sites	CEDD's Contractor	EIAO TM	Y	Y		۸
\$7.2.1.2	Existing trees of good quality and condition that are unavoidably affected by the works should be transplanted.	To minimise impact on existing trees	All relevant works sites	CEDD's Contractor	EIAO TM	Y	Y		N/A
\$7.2.1.2	Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.	To prevent unnecessary dust and dirt contaminating the air and adjacent areas.	All relevant works sites	CEDD's Contractor	EIAO TM		Y		۸
\$7.2.1.2	Construction plant and building material shall be orderly and carefully stored in order to create a neat and tidy visual appearance.	To mitigate potential visually obtrusive areas	All relevant works sites	CEDD's Contractor	EIAO TM		Y		۸
S7.2.1.2	Erection of decorative screen hoarding should be designed to be compatible with the existing urban context.	To mitigate and screen any potential visually obtrusive areas and enhance urban environment	All relevant works sites	CEDD's Contractor	EIAO TM		Y		۸
S7.2.1.2	All lighting in construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residences and GIC user. The contractor shall consider other security measures, which shall minimize the visual impacts.	To mitigate light pollution and adverse visual impacts on surrounding environment	All relevant works sites	CEDD's Contractor	EIAO TM		Y		۸
S7.2.1.2	Compensatory tree planting shall be incorporated along all roadside amenity areas affected by the construction works. The required numbers and locations of compensatory trees shall be determined and agreed with the Government during Tree Removal Application process under ETWB TCW No. 3/2006.	To reinstate and maximise compensatory tree numbers to equal or greater conditions	All relevant works sites	CEDD's Contractor	EIAO TM		Y		N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implei	nentatio	n Stages	Status
						D	С	0	
\$7.2.1.2	Compensatory tree planting shall be incorporated by the Project. The required numbers of compensatory trees shall follow the requirements of ETWB TCW No. 3/2006. Loss of amenity area adjacent to the Kwun Tong By-pass and planting areas in KTD South Apron will be mitigated by the creation of the Kai Tak South Apron: Amenity Area, which will be equal to or larger than the current provision.	To reinstate and maximise compensatory tree	All relevant works sites	CEDD's Contractor	EIAO TM		Y		N/A(1)
\$7.2.1.2	Trees and shrubs and climbers etc. shall be planted to soften and screen proposed roads, central strip and associated structure, and to enhance streetscape greening effect where appropriate.	To mitigate hard surfaces and hard standing landscape areas and to soften and enhance proposed design features	All relevant works sites	CEDD's Contractor	EIAO TM	Y		Y	N/A
S7.2.1.2	All works area, excavated area and disturbed area for tunnel construction and temporary road diversion or any other proposed works shall be reinstated to former conditions or better, with reasonable landscape treatment and to the satisfaction of the relevant Government departments.	To reinstate and maximise hard and soft landscape areas to equal or greater conditions	All relevant works sites	CEDD's Contractor	EIAO TM	Y		Y	N/A
S7.2.1.2	Tunnel portals and all above ground structures shall be sensitively designed to ensure the element with colour, texture and tonal quality being compatible to the existing urban context. Trees and shrub planting to minimize the potential adverse landscape and visual impacts shall be included where space permits. Roof top greening and vertical greening shall also be provided.	To mitigate hard surfaces and hard standing landscape areas and to soften and enhance proposed design features	All relevant works sites	CEDD's Contractor	EIAO TM	Y		Y	N/A
\$7.2.1.2	All works shall be carefully designed to minimize impacts on existing landscape resources and visually sensitive receivers. Existing trees within works area shall be retained and protected.	To minimise impact on existing trees	All relevant works sites	CEDD's Contractor	EIAO TM	Y		Y	N/A
S7.2.1.2	Existing trees of good quality and condition that are unavoidably affected by the works should be transplanted.	To minimise impact on existing trees	All relevant works sites	CEDD's Contractor	EIAO TM	Y		Y	N/A
Cultural Heritag	ge			•				<u> </u>	
S8.2.1.1 and 8.2.1.2	No culture heritage specific mitigation measures								

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Impler	mentatio	n Stages	Status
						D	С	0	
Waste Managem	ent Implication	I.	l.	I					
89.2.1.2	The requirements as stipulated in the ETWB TC(W) No.19/2005 Environmental Management on Construction Sites and the other relevant guidelines should be included in the Particular Specification for the future contractor as appropriate.	To keep trace of the generation, minimization, reuse and disposal of C&D materials	All areas / throughout construction period	Contractor	ETWB TC(W) No.19/2005		Y		N/A
S9.2.1.2	The future contractor should be requested to submit an outline Waste Management Plan (WMP) prior to the commencement of construction work, in accordance with the ETWB TC(W) No.19/2005 so as to provide an overall framework of waste management and reduction. The WMP should include: - Waste management policy; - Record of generated waste; - Waste reduction target; - Waste reduction programme; - Role and responsibility of waste management team; - Benefit of waste management; - Analysis of waste materials; - Reuse, recycling and disposal plans; - Transportation process of waste products; and - Monitoring and action plan.	To keep trace of the generation, minimization, reuse and disposal of C&D	All areas / throughout construction period	Contractor	ETWB TC(W) No.19/2005		Y		N/A(1)
S9.2.1.2	The waste management hierarchy should be strictly followed. This hierarchy should be adopted to evaluate the waste management options in order to maximise the extent of waste reduction and cost reduction. The records of quantities of waste generated, recycled and disposed (locations) should be properly documented.	To keep trace of the generation, minimization, reuse and disposal of C&D	All areas / throughout construction period	Contractor	ETWB TC(W) No.19/2005		Y		N/A(1)
S9.2.1.2	A trip-ticket system should be established in accordance with DevB TC(W) No. 6/2010 and Waste Disposal (Charges for Disposal of Construction Waste) Regulation to monitor the disposal of public fill and solid wastes at public filling facilities and landfills, and to control fly-tipping. A trip-ticket system would be included as one of the contractual requirements for the future contractor to strictly implement. The Engineer would also regularly audit the effectiveness of the system.	To monitor disposal of waste and control fly-tipping	All areas / throughout construction period	Contractor	DEVB TC(W) No. 6/2010		Y		N/A(1)

EM&A Ref.	Recommended Mitigation Measures		Implementation Agent					Relevant Standard or Requirement	Imple	mentatio	n Stages	Status
						D	С	0				
S9.2.1.2	A recording system for the amount of waste generated, recycled and disposed (locations) should be established. The future contractor should also provide proper training to workers regarding the appropriate concepts of site cleanliness and waste management procedures, e.g. waste reduction, reuse and recycling all the time.	To monitor disposal of waste and control fly-tipping	All areas / throughout construction period	Contractor	DEVB TC(W) No. 6/2010		Y		N/A(1)			
S9.2.1.2	The CEDD should be timely notified of the estimated spoil volumes to be generated and the PFC should be notified and agreement sort on the disposal of surplus inert C&D materials e.g. good quality rock during detailed design of the Trunk Road T2 Project. Wherever practicable, C&D materials should be segregated from other wastes to avoid contamination and to ensure acceptability at public filling areas or reclamation sites.	To monitor disposal of waste and control fly-tipping	All areas / throughout construction period	Contractor	DEVB TC(W) No. 6/2010		Y		N/A(1)			
S9.2.1.2	The extent of cutting operation should be optimised where possible. Earth retaining structures and bored pile walls should be proposed to minimise the extent of cutting.	To minimize, reuse and disposal of C&D materials	_	Contractor	DevB TC(W) No.6/2010		Y		N/A(1)			
S9.2.1.2	Inert C&D materials from road pavement would be reused for backfilling where possible	To minimize, reuse and disposal of C&D materials	_	Contractor	DevB TC(W) No.6/2010		Y		N/A(1)			
S9.2.1.2	TBM generated alluvium and other C&D materials should be treated at a slurry treatment plant prior to transferring to Public Fill Reception Facilities.	To minimize, reuse and disposal of C&D materials	TMB works area / during TBM works	Contractor	DevB TC(W) No.6/2010		Y		N/A			
S9.2.1.2	The site and surroundings should be kept tidy and litter free.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		۸			

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implen	nentation	n Stages	Status
						D	C	0	
S9.2.1.2	No waste is allowed to be burnt on site.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		۸
\$9.2.1.2	Make provisions in contract documents to allow and promote the use of recycled aggregates where appropriate.	To implement good site practice for handling, sorting reuse and recycling of wastes	Detailed Design	Design Consultant	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010	Y			N/A(1)
S9.2.1.2	Prohibit the future contractor to dispose of C&D materials at any sensitive locations e.g. natural habitat, etc. The future contractor should propose the final disposal sites in the WMP for approval before implementation.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		N/A(1)
S9.2.1.2	Stockpiled C&D materials should be covered by tarpaulin and/or watered as appropriate to prevent windblown dust and surface run off.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		۸
S9.2.1.2	Excavated C&D materials in trucks should be covered by tarpaulins to reduce the potential for spillage and dust generation.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		۸
S9.2.1.2	Wheel washing facilities should be used by all trucks leaving the site to prevent transferring mud trails onto public roads.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		۸
\$9.2.1.2	Excavated marine deposit (sediment) should be disposed of in a gazetted marine disposal ground under the requirements of the DASO or treated for backfilling.	To ensure proper disposal of marine sediment	All areas / throughout construction period	Contractor	ETWB TC(W) No.34/2002		Y		N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implen	nentation	n Stages	Status
						D	С	0	
S9.2.1.2	Standard formwork or pre-fabrication should be used as far as practicable to minimise the C&D materials arising. The use of more durable formwork or plastic facing for construction works should also be considered. The use of wooden hoardings should be avoided and metal hoarding should be used to facilitate recycling. Purchasing of construction materials should be carefully planned in order to avoid over-ordering and wastage.	To minimize, reuse and disposal of C&D materials	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		N/A(1)
\$9.2.1.2	The future contractor should recycle as many C&D materials as possible on-site. The public fill and C&D waste should be segregated and stored in separate containers or skips to facilitate the reuse or recycling of materials and proper disposal. Where practicable, the concrete and masonry should be crushed and used as fill materials. Steel reinforcement bar should be collected for use by scrap steel mills. Different areas of the sites should be considered for segregation and storage activities.	To minimize, reuse and disposal of C&D materials	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		^
\$9.2.1.2	All falsework should be steel instead of wood as far as practicable.	To minimize, reuse and disposal of C&D materials	All areas / throughout construction period	Contractor	DevB TC(W) No.6/2010		Y		N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Impler	nentatio	n Stages	Status
						D	С	0	
S9.2.1.2	Chemical waste producers should register with the EPD and chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows: - Suitable for the substance to be held, resistant to corrosion, maintained in good conditions and securely closed; - Having a capacity of <450L unless the specifications have been approved by the EPD; and - Displaying a label in English and Chinese according to the instructions prescribed in Schedule 2 of the Regulations Clearly labelled and used solely for the storage of chemical wastes; - Enclosed with at least 3 sides; - Impermeable floor and bund with capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest; - Adequate ventilation; - Sufficiently covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and - Incompatible materials are adequately separated.	chemical waste within works sites and works areas	All areas / throughout construction period	Contractor	Code of Practice on the Packaging, Handling and Storage of Chemical Wastes		Y		A
S9.2.1.2	Waste oils, chemicals or solvents should not be disposed of to drain.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	EIAO TM		Y		۸

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Impler	nentatio	n Stages	Status
						D	С	0	
S9.2.1.2	Adequate numbers of portable toilets should be provided for on-site workers. Portable toilets should be maintained in reasonable states, which will not deter the workers from utilising them. Night soil should be regularly collected by licensed collectors.	To ensure proper disposal of sewage sludge	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		N/A(1)
S9.2.1.2	General refuse arising on-site should be stored in enclosed bins or compaction units separately from C&D and chemical wastes. Sufficient dustbins should be provided for storage of waste as required under the Public Cleansing and Prevention of Nuisances By- laws. In addition, general refuse should be cleared daily and disposed of to the nearest licensed landfill. Burning of refuse on construction sites is prohibited.	To separate the general refuse from other waste types and proper disposal of the refuse	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance		Y		^
S9.2.1.2	All waste containers should be in a secure area on hardstanding.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance		Y		۸
\$9.2.1.2	Aluminium cans should be collected and recovered from the waste stream by reputable collectors if they are segregated and easily accessible. Separately labelled bins for their deposition should be provided as far as practicable.	To implement on-site sorting facilitating reuse and recycling of materials as well as proper disposal of waste	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance		Y		N/A(1)
\$9.2.1.2	Office wastes can be reduced by recycling of paper if such volume is sufficiently large to warrant collection. Participation in a local collection scheme by the future contractor should be advocated. Waste separation facilities for paper, aluminium cans, plastic bottles, etc should be provided on-site.	To separate the general refuse from other waste types and proper disposal of the refuse	/ throughout construction	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance		Y		N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implen	nentatio	n Stages	Status
						D	С	0	
S9.2.1.2	Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including waste reduction, reuse and recycling.	To implement good site practice for handling, sorting reuse and recycling of wastes	Contract Mobilisation	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance		Y		N/A(1)
S9.2.1.2	During construction phase, regular site inspections and supervision of the waste management procedures shall be undertaken as part of the EM&A procedures.	To ensure proper control, all waste is removed from site areas as appropriate and illegal disposal of waste is not being undertaken	All areas / throughout construction period	Contractor	EIAO TM		Y		۸

Remarks: EM&	&A Programme under EP-451/2013
D	Design
С	Construction
Y	Yes
О	Operation
^	Compliance of mitigation measure;
N/A	Not applicable at this stage;
N/A(1)	Not observed;
*	Recommendation was made during site audit but improved/retified by the contractor;
#	Recommendation was made during site audit but not yet improved/retified by the contractor;
X	Non-compliance of mitigation measure;
•	Non-compliance but rectified by the contractor.

APPENDIX L SUMMARIES OF ENVIRONMENTAL COMPLAINT, WARNING, SUMMON AND NOTIFICATION OF SUCCESSFUL PROSECUTION

Contract No. ED/2018/04 Trunk Road T2 and Infrastructure Works for Development at the Former South Apron

Reporting Month: June 2022

Log Ref.	Location	Received Date	Details of Complaint/war ning/summon and prosecution	Investigation/Mitigation Action	Status
-	-	_	-	-	-

Remarks:

No environmental complaint/warning/summon and prosecution were received in the reporting period.

APPENDIX M SUMMARY OF EXCEEDANCE

Environmental Permit No.: EP-451/2013 Environmental Team for Trunk Road T2

Appendix M – Summary of Exceedance

Reporting Month: June 2022

(A) Exceedance Report for Air Quality

No Action Level and Limit Level exceedance of 24hr TSP monitoring was recorded in this reporting month.

(B) Exceedance Report for Construction Noise

Action Level for Construction Noise


No Action Level exceedance was recorded due to the documented complaint received in this reporting month.


Limit Level for Construction Noise


No exceedance for daytime construction noise monitoring was recorded in the reporting month.


(C) Summary of Landscape and Visual Non-Conformity (NIL in the reporting month)


APPENDIX N TENTATIVE CONSTRUCTION PROGRAMME

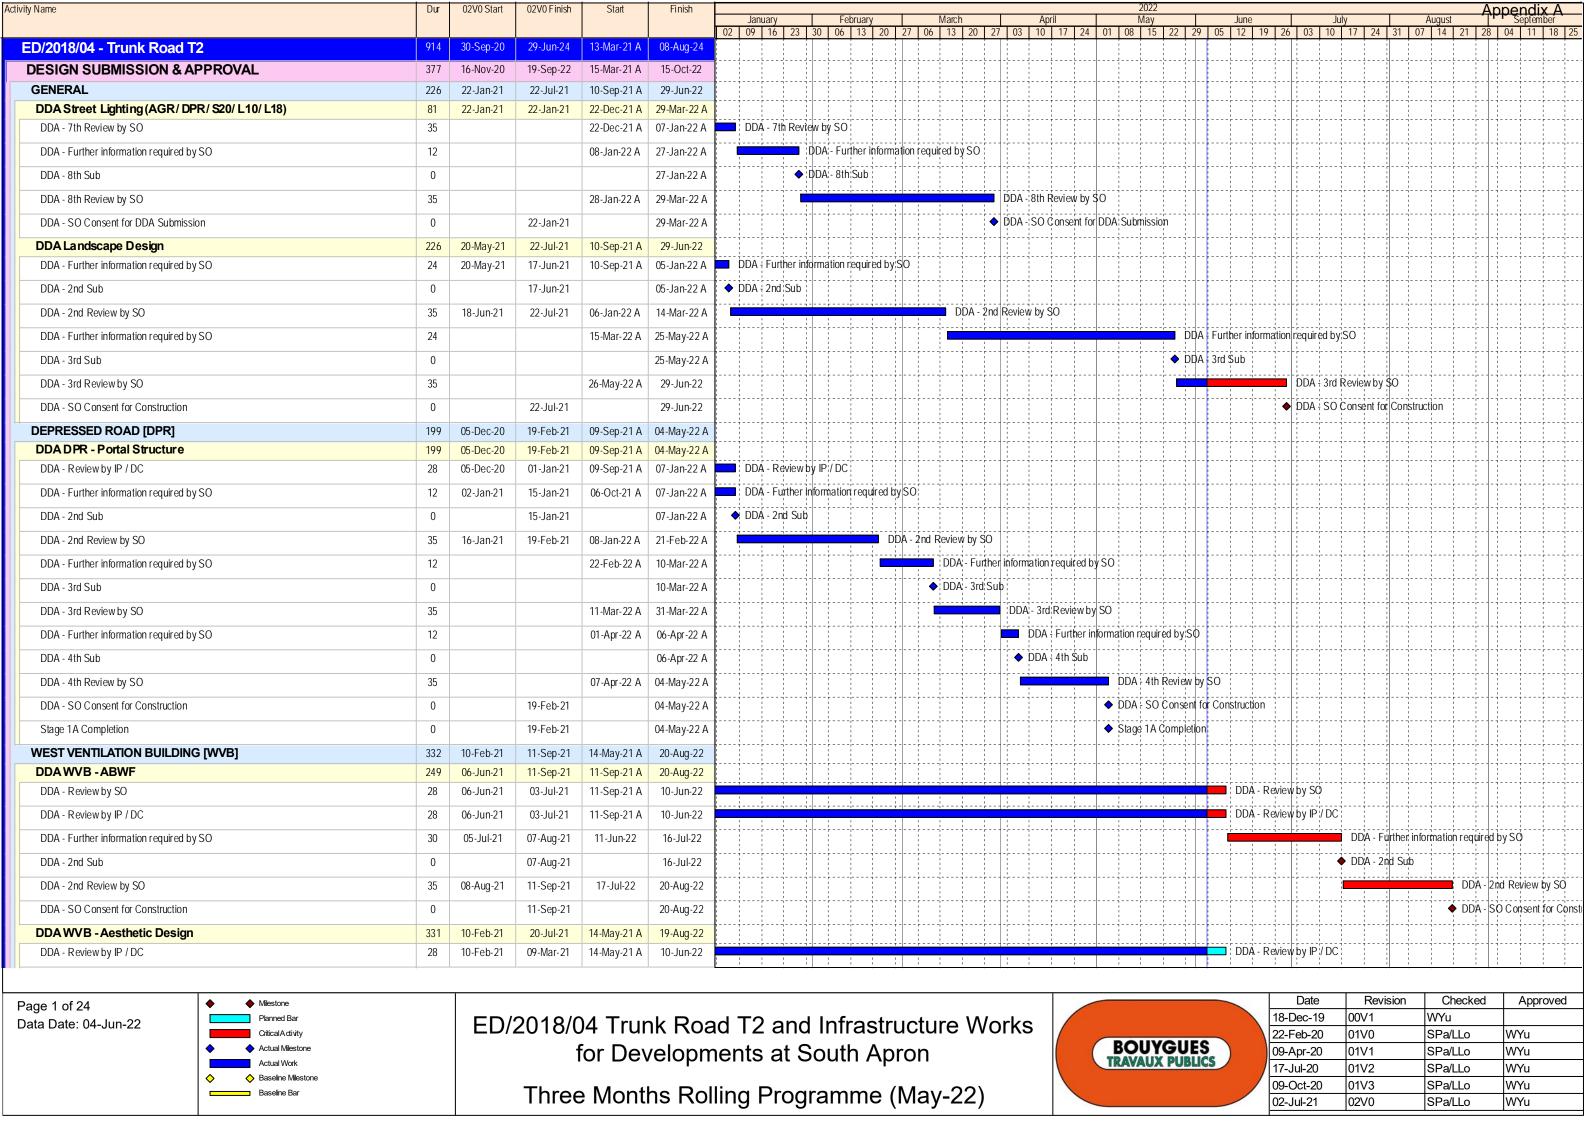


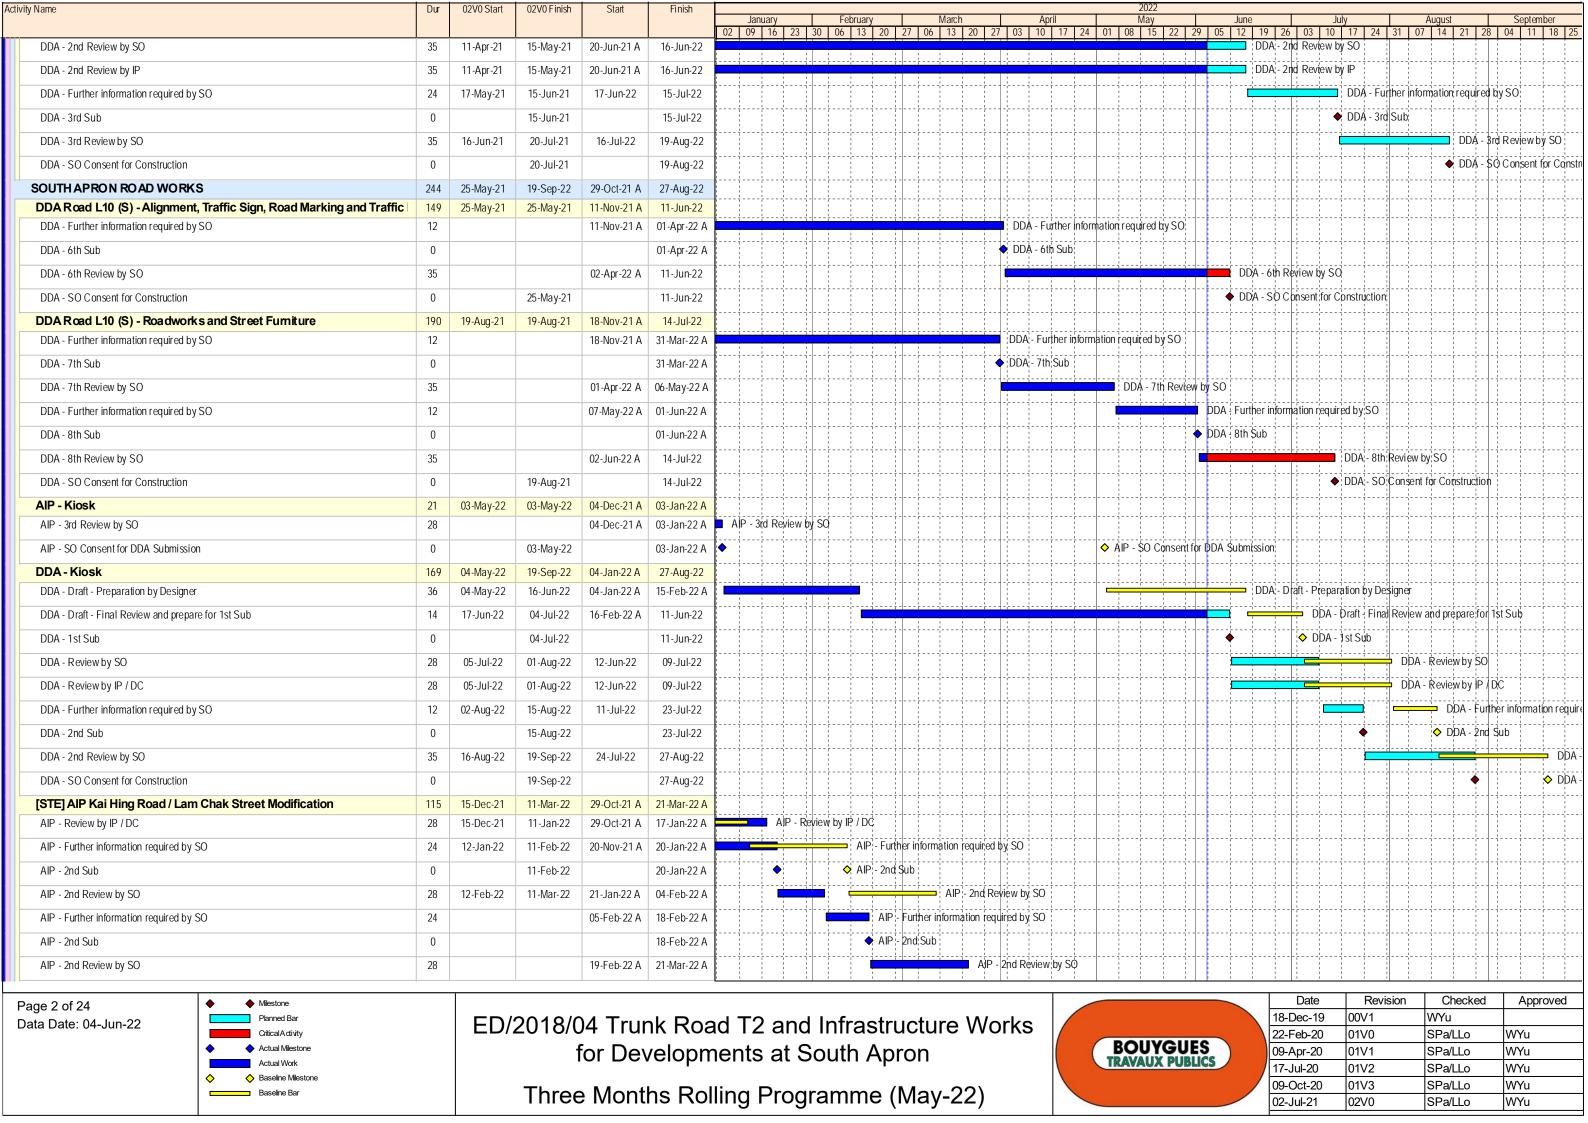


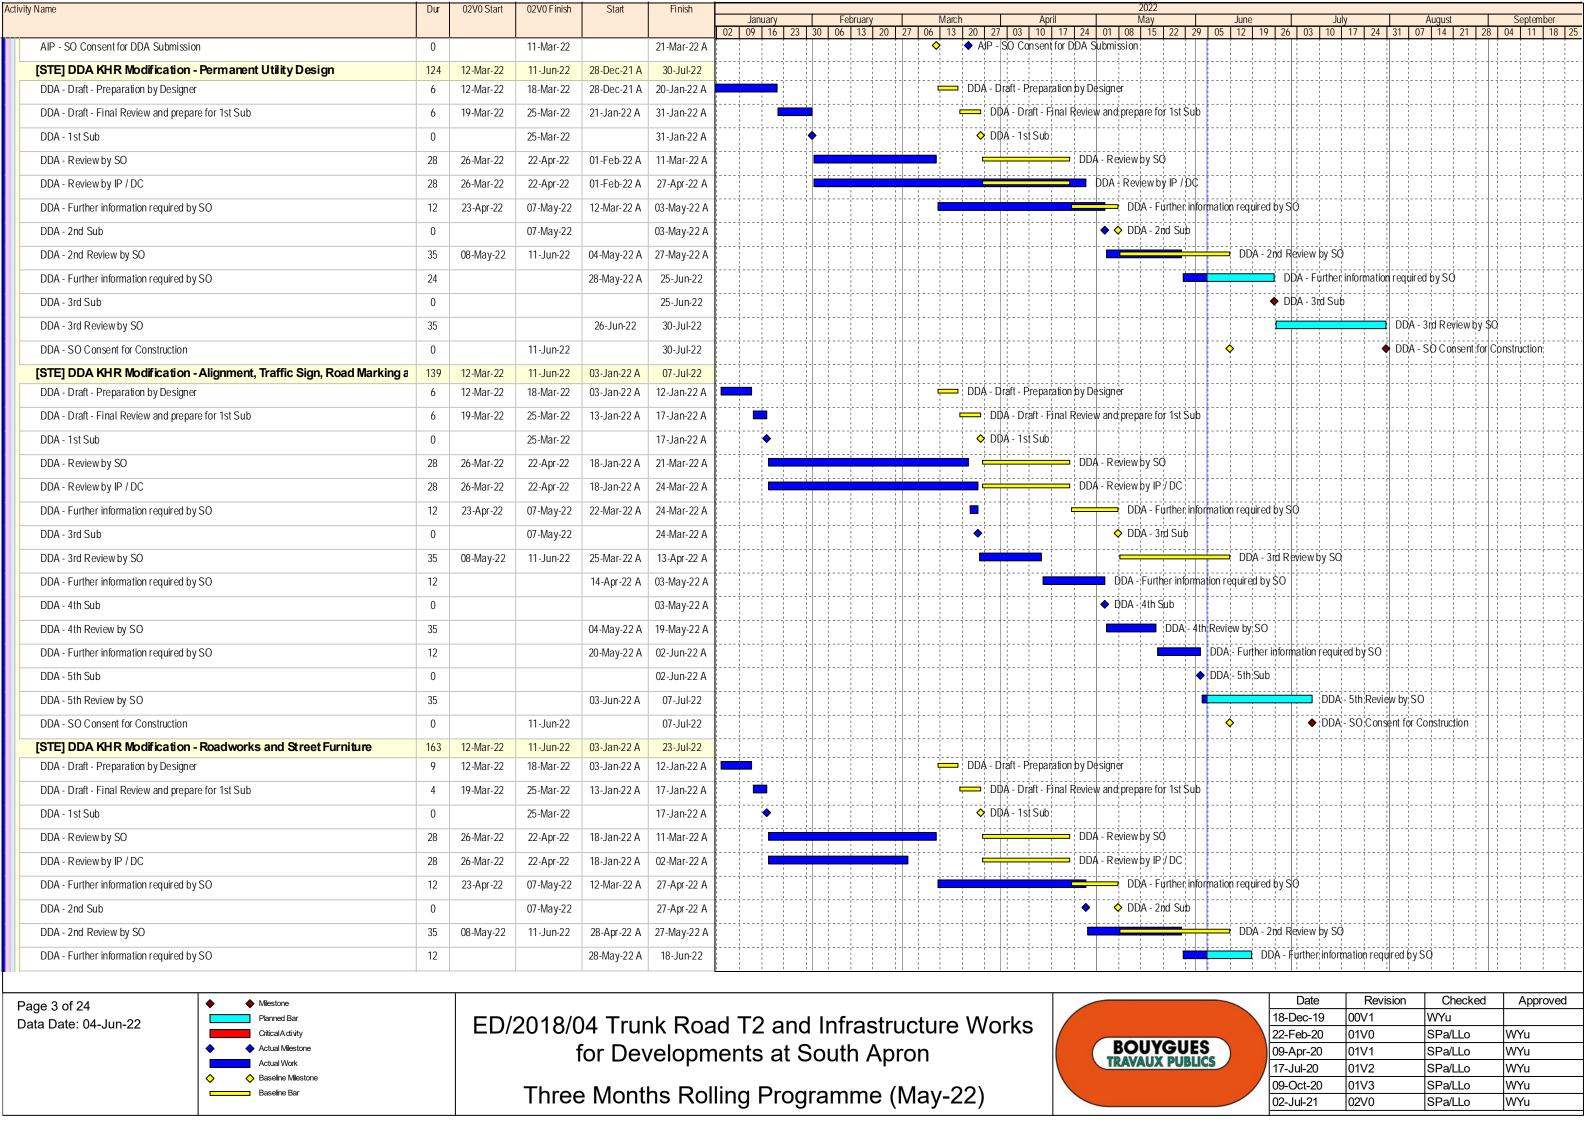


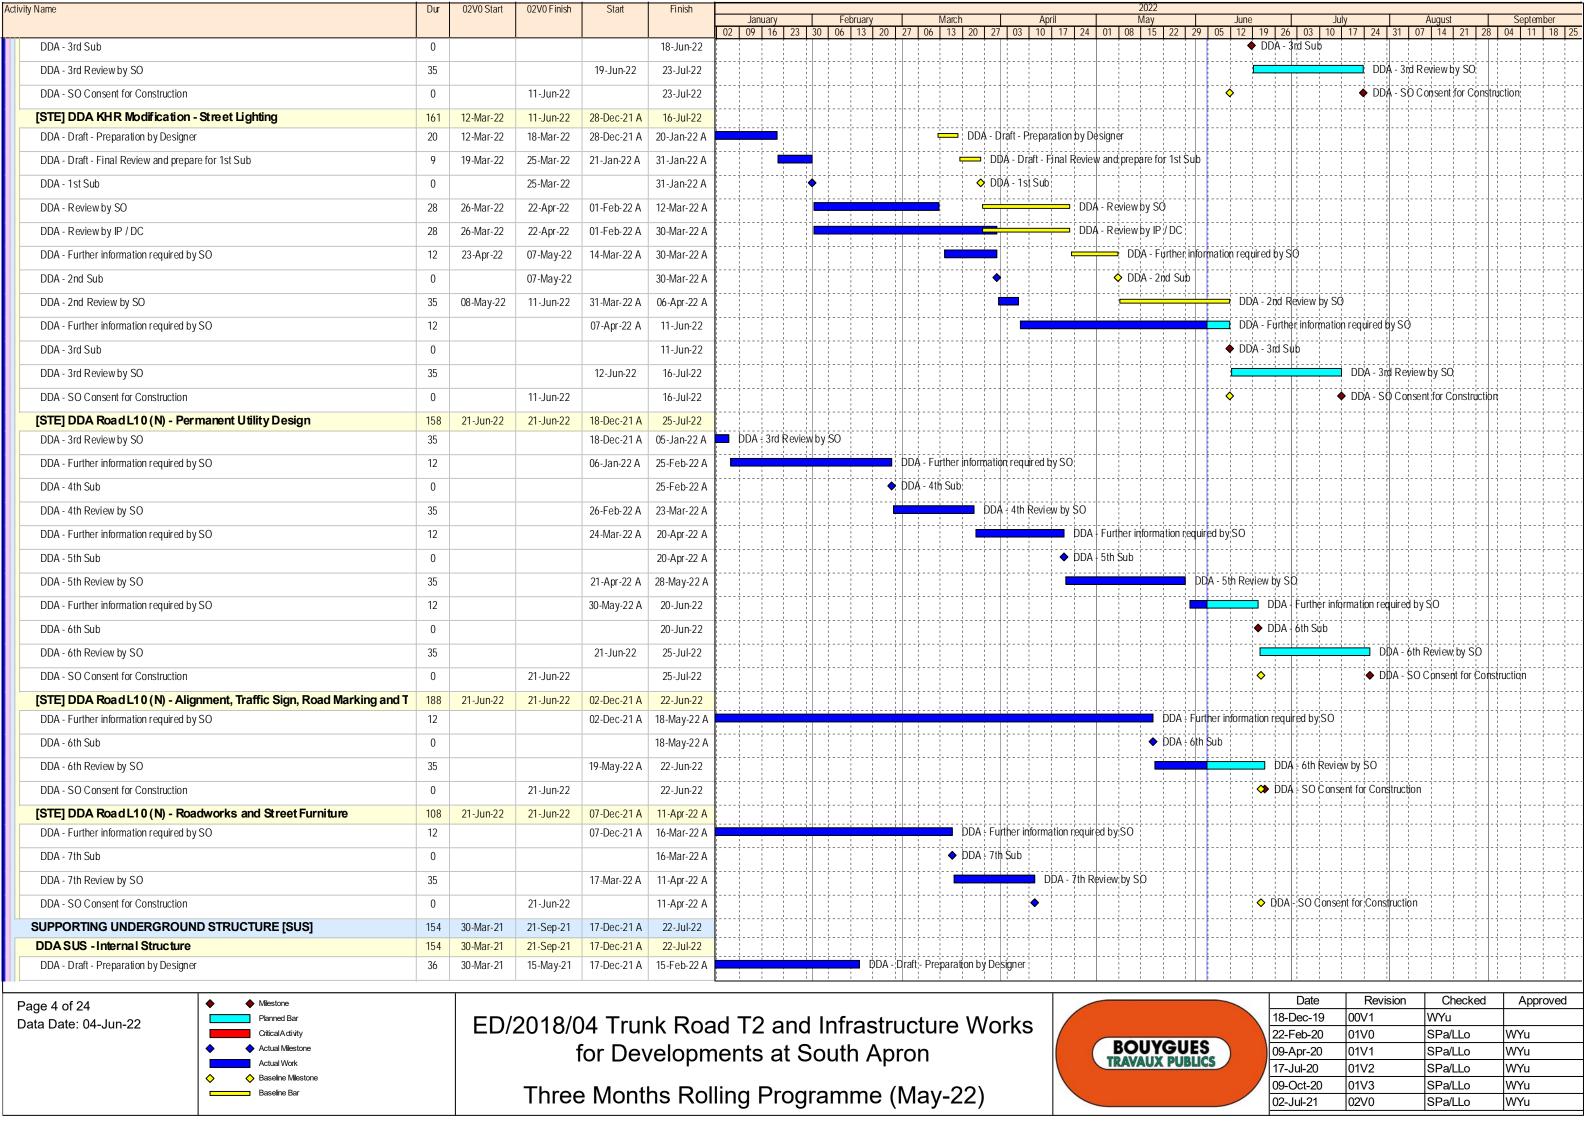

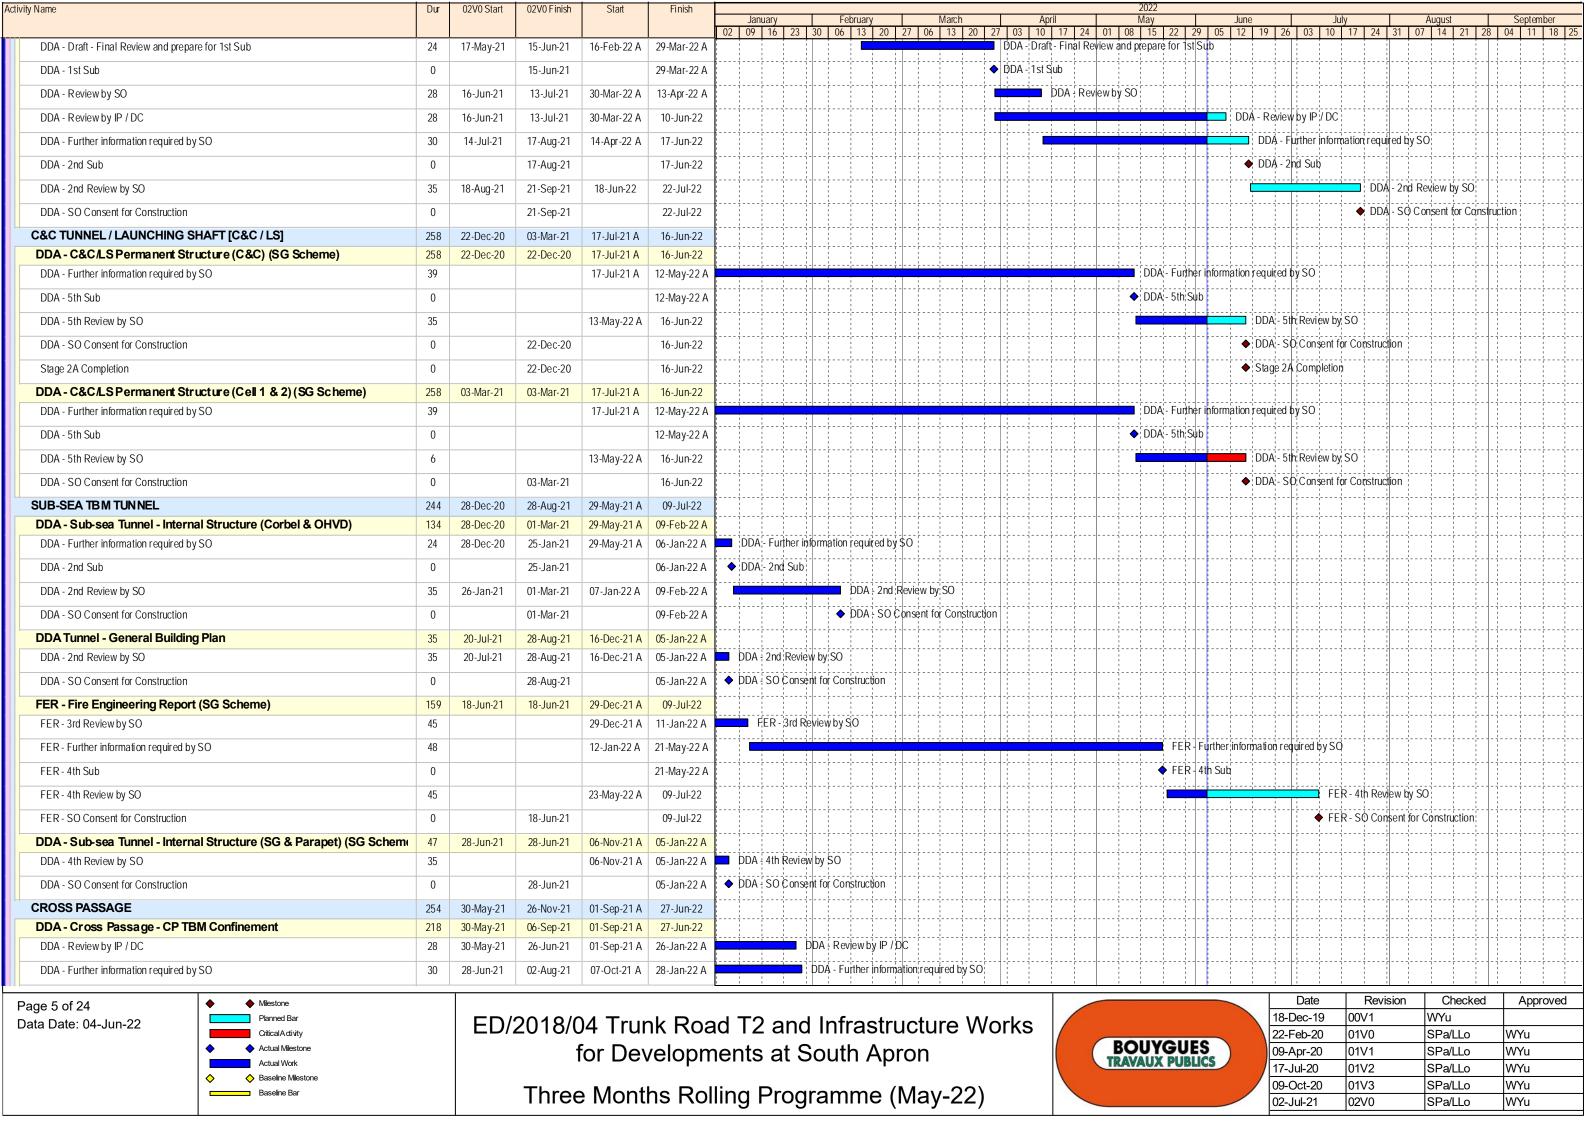

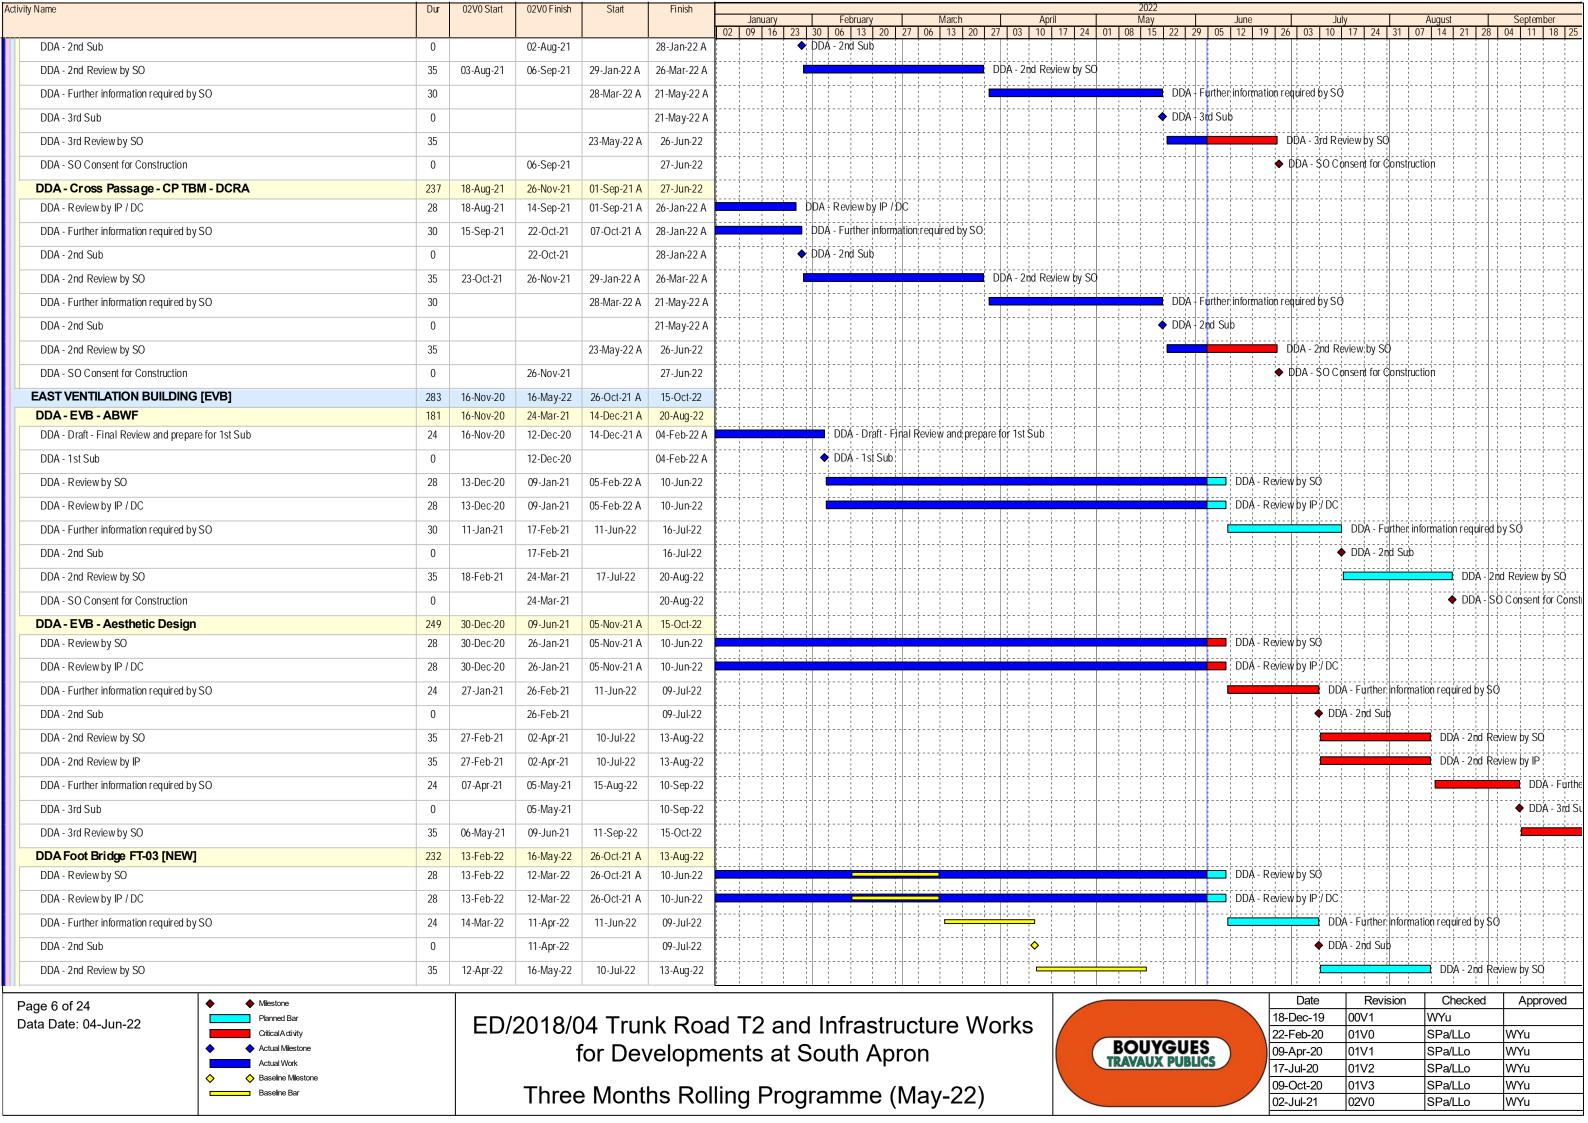

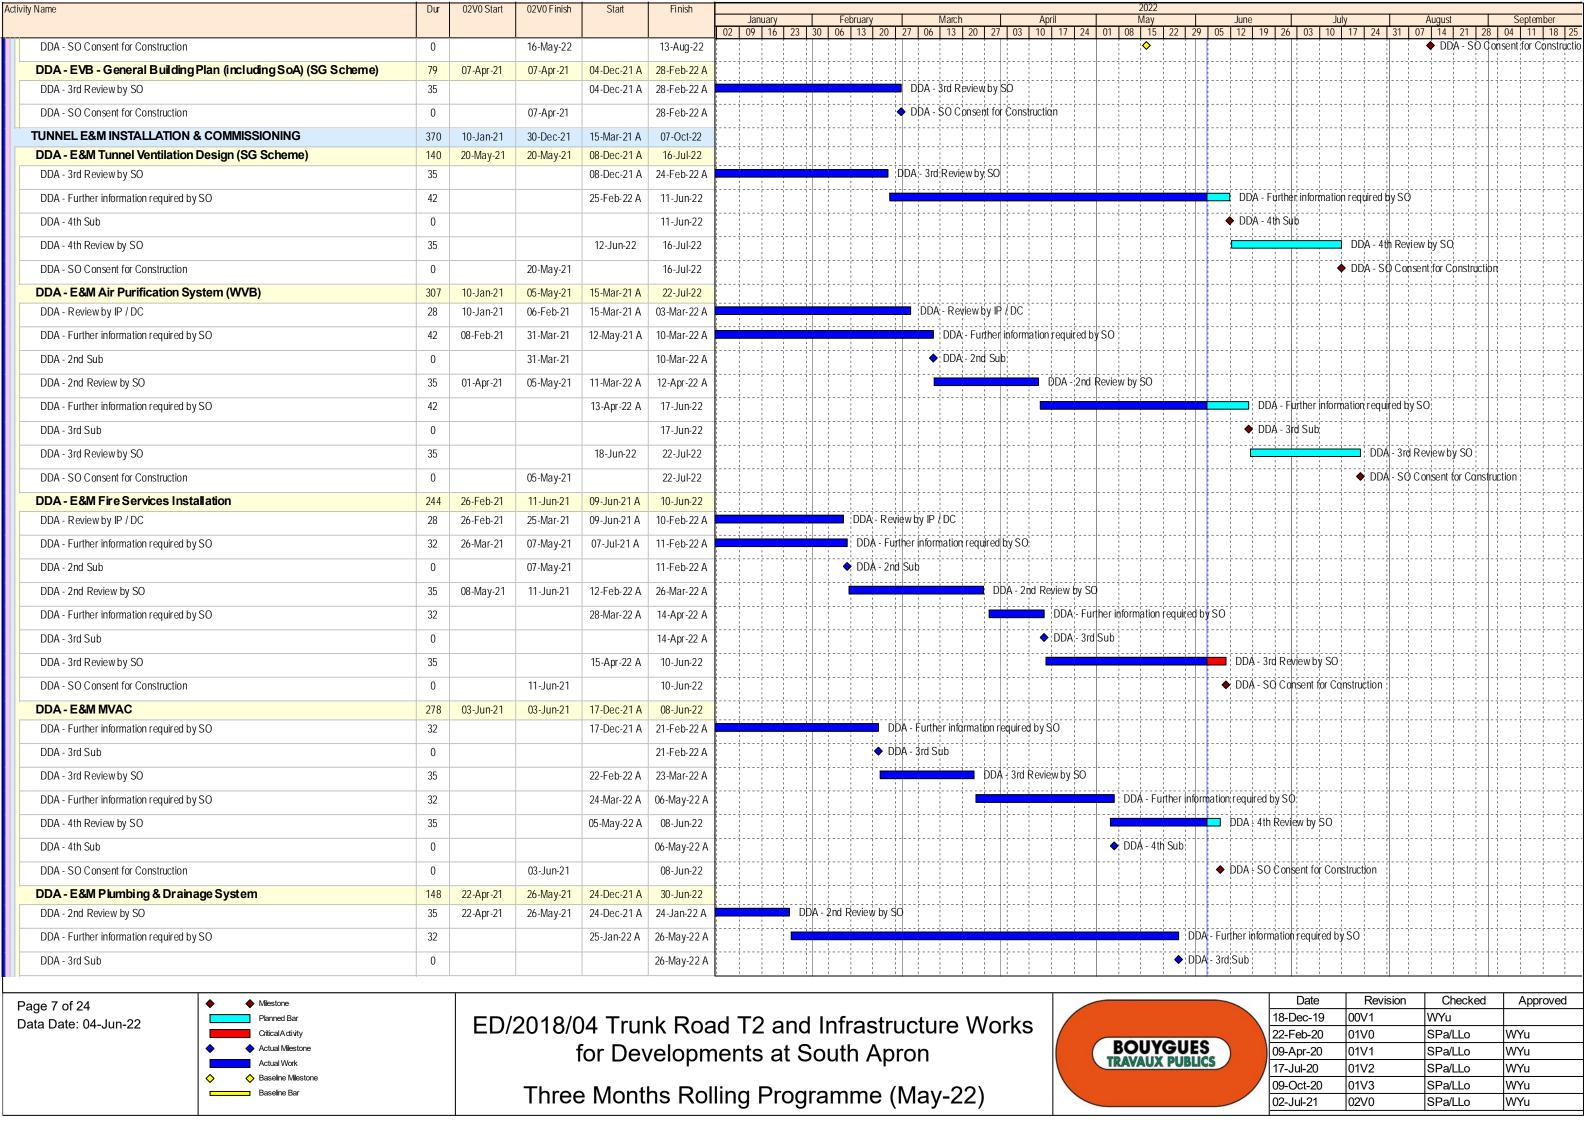


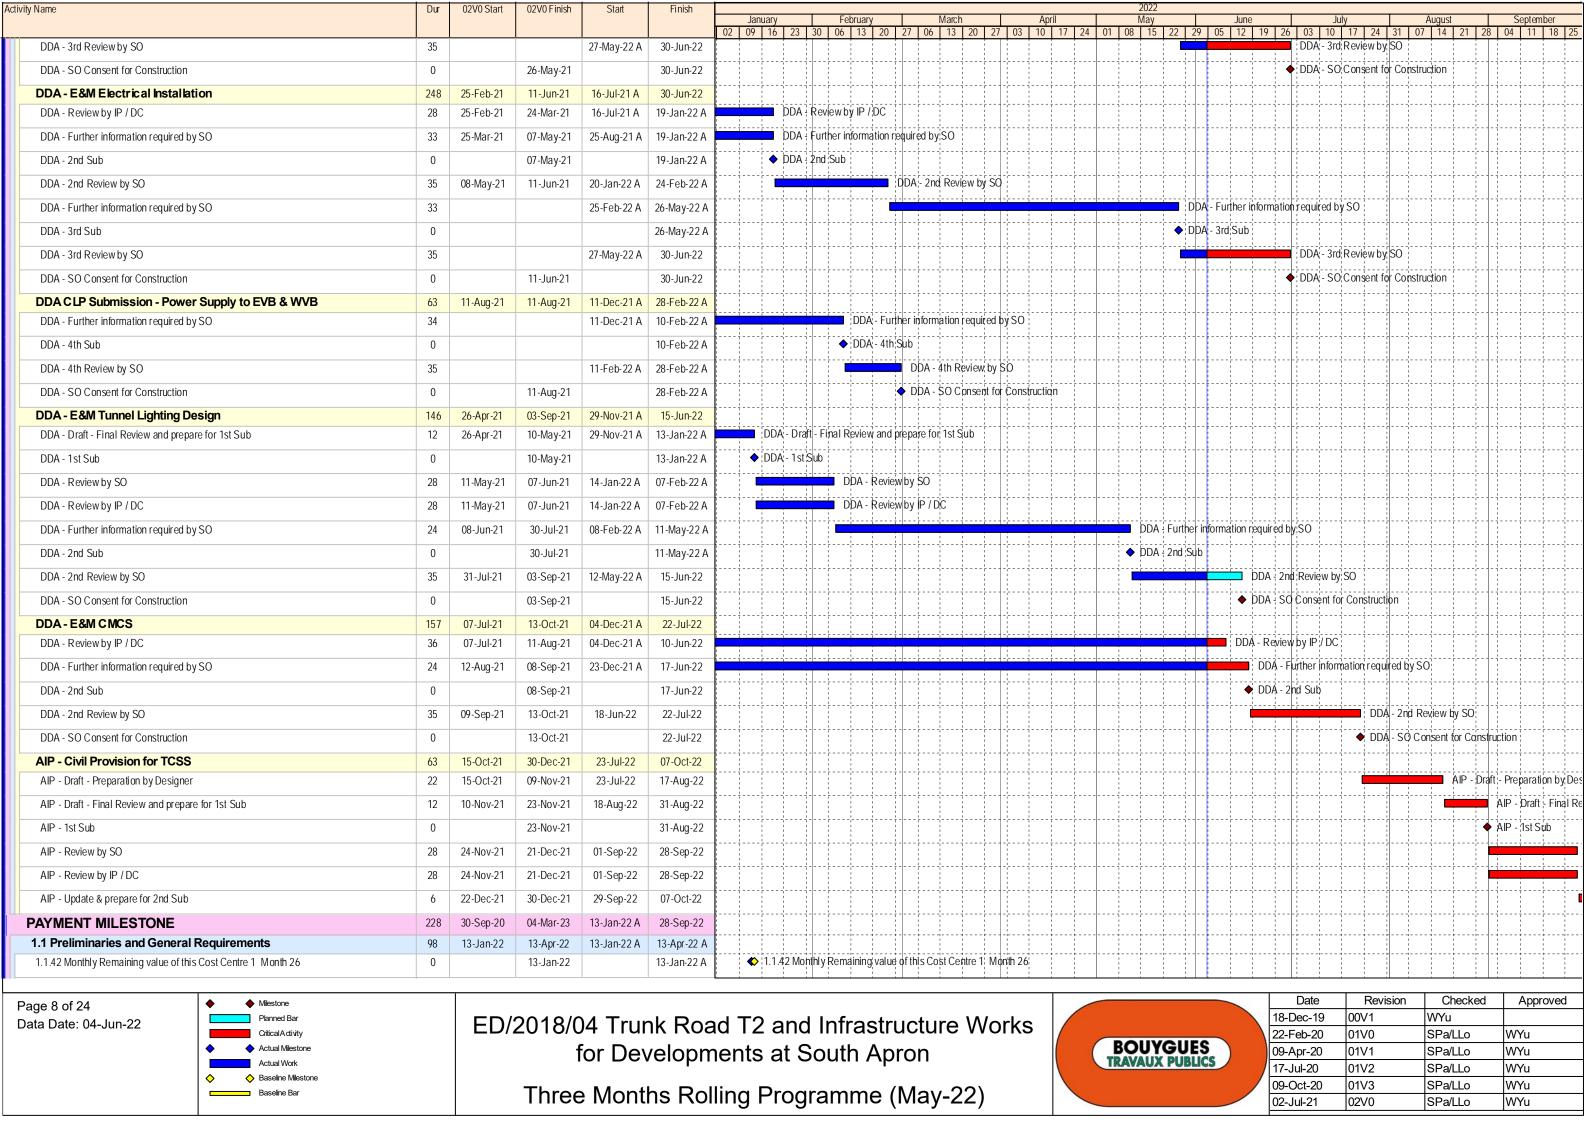



Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2022
						January February March April May June July August September O2 O9 16 23 30 06 13 20 27 06 13 20 27 03 10 17 24 01 08 15 22 29 05 12 19 26 03 10 17 24 31 07 14 21 28 04 11 18 25
1.1.42 Monthly Remaining value of this Cost Centre 1 Month 27	0		14-Feb-22		14-Feb-22 A	→ 1,1.42 Monthly Remaining value of this Cost Centre 1 Month 27
1.1.42 Monthly Remaining value of this Cost Centre 1 Month 28	0		14-Mar-22		14-Mar-22 A	◆ 1.1.42 Monthly Remaining value of this Cost Centre 1 Month 28
1.1.42 Monthly Remaining value of this Cost Centre 1 Month 29	0		13-Apr-22		13-Apr-22 A	♦ 1.1.42 Monthly Remaining value of this Cost Centre 1 Month 29
3.1 for Trunk Road T2	138	29-Mar-21	21-Sep-21	13-Jan-22 A	22-Jul-22	
3.1 .50 Approval AIP for completion of SUS	0		29-Mar-21		13-Jan-22 A	◆ 3.1.50 Approval AIP for completion of SUS
3.1 .52 Approval DDA for completion of SUS	0		21-Sep-21		22-Jul-22	◆ 3.1 ,52 Approval D DA for completion of SUS
3.3 for the Remaining Stage 5 Infrastructure Works - Road L10 (Southe	0	26-Feb-21	26-Feb-21	13-Jan-22 A	13-Jan-22 A	
3.3 .16 Approval DDA for waterworks	0		26-Feb-21		13-Jan-22 A	◆ 3.3 .1;6 Approval DDA for waterworks
3.4 for the Remaining Stage 5 Infrastructure Works - FT02	51	09-Mar-21	09-Mar-21	13-Jan-22 A	14-Mar-22 A	
3.4 .10 Approval DDA for modification of existing footbridge	0		09-Mar-21		13-Jan-22 A	♦ 3.4.10 Approval DDA for modification of existing footbridge:
3.4 .12 Approval Demolition plan for existing footbridge	0		09-Mar-21		14-Mar-22 A	◆ 3.4.12;Approval Demolition plan for existing footbridge
3.4 .13 Complete whole activities of this cost centre	0		09-Mar-21		14-Mar-22 A	♦ 3.4 .13 Complete whole activities of this cost centre
3.5 for Lam Chak Street and Kai Hing Road	6	11-Jun-22	11-Jun-22	23-Jul-22	30-Jul-22	
3.5 .8 Approval DDA for roadworks	0		11-Jun-22		23-Jul-22	♦ 3.5 8 Approval DDA for toadworks
3.5 .24 Approval DDA for landscape works	0		11-Jun-22		23-Jul-22	♦ 3.5; 24 Approval DDA for landscape works
3.5.25 Complete whole activities of this cost centre	0		11-Jun-22		23-Jul-22	♦ 3.5 25 Complete whole activities of this cost centre
3.5 .12 Approval DDA for stormwater drainage works	0		11-Jun-22		30-Jul-22	♦ 3.5;.12 Approval D.DA for stormwater drainag
3.5 .16 Approval DDA for waterworks	0		11-Jun-22		30-Jul-22	♦ 3.5.16 Approval D DA for waterworks
3.5 .20 Approval DDA for sewage works	0		11-Jun-22		30-Jul-22	♦ 3.5, 20 Approval D.DA for sewage works
3.6 for Road L10 (Northern Section)	0	21 Jun 22		04-Jun-22	04-Jun-22	s.seo/ppotato/nlossenige waits
3.6 .8 Approval DDA for Road L10 (northern section)	0	21-Jun-22	21-Jun-22 21-Jun-22	04-Jun-22	04-Jun-22*	◆ ◆ 3,6.8 Approval DDA for Road L10 (northern; section)
3.6.9 Complete whole activities of this cost centre	0		21-Jun-22		04-Jun-22*	◆ ♦ 3,6.9 Complete whole activities of this cost centre
	0	20.0 20		04 lun 22		▼ ↓ J. J. Somplete whole, activities by this bost territory
3.9 for the Pipelines for District Cooling System for Commissioning of a 3.9.11 Submit O&M manual for DCS pipelines	0	30-Sep-20	30-Sep-20 30-Sep-20	04-Jun-22	04-Jun-22 04-Jun-22	◆ 3.9;11 Submit;0&M manual for DC\$ pipelines
4.2 Depressed Road and Remaining Ventilation Adits at the South Apro	0	20-Apr-21	14-Sep-21	04-Jun-22	04-Jun-22	4 S. 7.1 Spinned Williams Co. Declared in the control of the contr
4.2 .17 Complete South Apron Adist permanent structure 1	0	20-Αμι-21	31-Aug-21	04-Juli-22	04-Jun-22*	◆ 4.2.17 Complete South Apron Adist permanent structure 1
4.2 .23 Complete foundation of Depressed Road by length 1	0		20-Apr-21		04-Jun-22*	◆ 4.2.23 Complete foundation of Depressed Road by length 1
4.2 .31 Complete permanent structure of Depressed Road by length 1	0					◆ 4.2.31 Complete permanent structure of Depressed Road by length 1
	_	47.11 04	14-Sep-21	04.1.00	04-Jun-22*	▼ 4.2.5 i Complete permanent structure or prepressed Roati by tengin i
5.2 Completion of SUS 5.2 .29 Complete remaining works in SUS by length 0.5	93	17-Nov-21	06-Apr-22 17-Nov-21	04-Jun-22	24-Sep-22 04-Jun-22	◆ 5.2, 29 ¢omplete remaining works in SU\$ by length;0.5
	0					◆ 5.2;30 Complete remaining works in SUS by length 0.6
5.2 .30 Complete remaining works in SUS by length 0.6	0		31-Dec-21		18-Jun-22	
5.2 .31 Complete remaining works in SUS by length 0.7	0		16-Feb-22		01-Aug-22	♦ 5.2 .31 Complete remaining works in SUS b
5.2 .5 Complete overhead ventilation duct slab by length 0.1	0		07-Feb-22		05-Aug-22	◆ 5.2 .5 Complete overhead ventilation duc
5.2 .6 Complete overhead ventilation duct slab by length 0.2	0		23-Feb-22		22-Aug-22	♦ 5.2.6 Comptete overhead v
5.2 .15 Complete Thermal barrier by length 0.1	0		25-Feb-22		24-Aug-22	◆ 5.2 .15 Complete Thermal
5.2 .7 Complete overhead ventilation duct slab by length 0.3	0		11-Mar-22		07-Sep-22	◆ 5.2.7;Complete
5.2 .32 Complete remaining works in SUS by length 0.8	0		30-Mar-22		13-Sep-22	◆ 5.2.32 Cor
5.2 .20 Complete Thermal barrier by length 0.6	0		06-Apr-22		19-Sep-22	♦ 5.2.20
5.2 .8 Complete overhead ventilation duct slab by length 0.4	0		28-Mar-22		24-Sep-22	♦ 5.1
5.2 .16 Complete Thermal barrier by length 0.2	0		28-Mar-22		24-Sep-22	♦ 5.1
6.2 TBM Tunnel	21	23-Mar-22	21-Apr-22	24-Aug-22	19-Sep-22	[
6.2 .7 Complete excavation & installation of TBM Tunnel lining by length 0.35	0	20 .viui 22	23-Mar-22		24-Aug-22	♦ 6.2 7;Complete excavatio
					ŭ	Date Revision Checked Approved
Page 9 of 24 Data Date: 04-Jun-22			201010	\/ T <u>~</u>	sk Daa	40 Dec 40 100/4 140/4
CriticalActivity				_		ad 12 and initiastructure vvorks
◆ Actual Milestone Actual Work			1	tor Dev	/elopm	nents at South Apron BOUYGUES 09-Apr-20 01V1 SPa/LLo WYu 17-Jul-20 01V2 SPa/LLo WYu SPa/LLo WYu SPa/LLo WYu SPa/LLo
♦ Baseline Milestone			- .			17-301-20 01V2 9F4/LLO WYU
Baseline Bar			Ihree	e Mont	ns Rol	lling Programme (May-22)
		<u> </u>				


Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	nish										Sont	ember					
						02 09 16 23 3	30 06 13 2	20 2	7 06 13 20	27 03	10 17	24 01 08	15 22		12 19	26 03 1	0 17 24	31 0)7 14	21 28	04 1	1 18 25
6.2 .8 Complete excavation & installation of TBM Tunnel lining by length 0.4	0		07-Apr-22		07-Sep-22	; ;;;;;;;;					¦									ļ		.8 Complete
6.2 .24 Complete TBM Tunnel waterproofing 0.4	0		07-Apr-22		07-Sep-22	<u> </u>					<u> </u>										♦ 6.2	.24 Comple
6.2 .9 Complete excavation & installation of TBM Tunnel lining by length 0.45	0		21-Apr-22		19-Sep-22						\Q									ļļ		♦ 6.2.9
6.3 Cross Passages for TBM Tunnel	34	07-Apr-22	23-May-22	18-Aug-22	28-Sep-22	; ;;;;;;;														 		
6.3 .5 Complete Ground treatment for all Cross Passages 0.2	0		07-Apr-22		18-Aug-22	<u> </u>				· . • ;										ļļ		ound treatm
6.3 .14 Complete excavation and support of Cross Passages 0.1	0		23-Apr-22		31-Aug-22	<u> </u>					ļ									1	6.3 .14 C	omplete exc
6.3 .6 Complete Ground treatment for all Cross Passages 0.3	0		23-May-22		28-Sep-22								>									•
7.1 Western Ventilation Building	0	26-Feb-22	26-Feb-22	04-Jun-22	04-Jun-22	; ;;;;;;;;					¦ 									<u> </u> 		
7.1 .5 Complete pile foundation for WVB 0.5	0		26-Feb-22		04-Jun-22			\			¦						tion for WVE	.1		} }		
7.1 .6 Complete pile foundation for WVB 1	0		26-Feb-22		04-Jun-22			\Q						♦ 7.1.6	6 Complete	pile founda	tion for WVE	3 1		ļ		
8.1 Eastern Ventilation Building	0	14-Jun-22	14-Jun-22	28-Sep-22	28-Sep-22	 					ļ 											
8.1.3 Complete excavation for EVB 1	0		14-Jun-22		28-Sep-22	; ;;;;;;;					¦									ļ 		
9.1 Launching Shaft	21	01-Jun-22	16-Jun-22	08-Aug-22	01-Sep-22			· 			 -									Complete		
9.1 .20 Complete permanent wall & bottom slab for Launching Shaft by length 0.6	0		01-Jun-22		08-Aug-22						ļļ.									LL	. J I	nt wall & bo
9.1.18 Complete permanent wall & bottom slab for Launching Shaft by length 0.2	0		01-Jun-22		18-Aug-22	<u> </u>					¦			♦						L		ermanent w
9.1 .21 Complete permanent wall & bottom slab for Launching Shaft by length 0.8	0		16-Jun-22		22-Aug-22										♦							e permaner
9.1 .22 Complete permanent wall & bottom slab for Launching Shaft by length 1	0		16-Jun-22		22-Aug-22										♦					◆ 9.1 .2	2 Comple	e permaner
9.1 .19 Complete permanent wall & bottom slab for Launching Shaft by length 0.4	0		16-Jun-22		01-Sep-22										♦						9.1.19	Complete pe
11.1 Drill and Break Tunnel	153	13-Aug-21	25-Jan-22	12-Feb-22 A	03-Sep-22																	
11.1.2 Complete tunnel excavation 0.3 by length	0		13-Aug-21		12-Feb-22 A		♦ 11.1.2	Comp	olete tunnel excav	ation 0.3 by	length											
11.1.2 Complete tunnel excavation 0.4 by length	0		14-Sep-21		13-May-22 A							•	11.1.2 Co	mplete tunn	el excavati	on 0.4 by le	ngth					
11.1.2 Complete tunnel excavation 0.5 by length	0		19-Oct-21		04-Jun-22*									♦ 11.1.	2 Complet	e tunnel exc	avation 0.5	by length				
11.1.3 Complete tunnel excavation 0.6 by length	0		19-Nov-21		04-Jun-22*									♦ 11.1.	.3 Complet	e tunnel exc	avation 0.6	by length				
11.1.5 Complete tunnel excavation 0.7 by length	0		21-Dec-21		04-Jun-22*	;;;;;;; -		· 			ii		-	♦ 11.1.	5 Complet	e tunnel exc	avation 0.7	by length				
11.1.7 Complete tunnel excavation 0.8 by length	0		25-Jan-22		03-Sep-22	♦															11.1.7	Complete tu
12.1 Drill and Blast Tunnel	177	14-Feb-22	31-Mar-22	14-Mar-22 A	13-Apr-22 A	 		·		+										}		
12.1.10 Complete tunnel excavation 0.9 by length	0		14-Feb-22		14-Mar-22 A		\Q		♦ 12.1.1	0 Complete	tunnel exca	vation 0.9 by le	ngth									
12.1.11 Complete tunnel excavation 1 by length	0		31-Mar-22		13-Apr-22 A	{ ; ; ; ; -				\	♦ 12.1.11	Complete tun	nel excavat	on 1 by len	gth					;; 	·	
13.1 Lam Tin Interchange Works	51	20-Jun-22	19-Aug-22	20-Jun-22	19-Aug-22																	
13.1 .1 Complete foundation	0		20-Jun-22		20-Jun-22*										♦ 13.	1.1 Comple	te foundatio	n				
13.1 .2 Complete fabrication of structural frame	0		19-Aug-22		19-Aug-22*	{ ; ; ; -		-			iii								\Q	13.1 .2 (Complete	abrication o
14.3 Kiosks	77	20-Jun-22	20-Sep-22	20-Jun-22	20-Sep-22	{ ; ; ; -					 -											
14.3.1 Complete fabrication and application of protective systems for structural frame of	0		20-Jun-22		20-Jun-22*										◇ 14.	3.1 Comple	1 1		1	1 1 1	1 1	s for structu
14.3.2 Complete erection of structural frame of kiosk 1	0		20-Jul-22		20-Jul-22*												♦ 14.3	.2 Comp	1	!!!	1 1	me of klosk
14.3.3 Complete cladding of kiosk 1	0		20-Aug-22		20-Aug-22*	,					, 								<	14.3.3	Complete	cladding of
14.3 .4 Complete architectural works and finishing of kiosk 1	0		20-Sep-22		20-Sep-22*						 -										- 	♦ 14.3.
15.0 E&M Design Works	86	10-May-21	03-Sep-21	13-Jan-22 A	15-Jun-22															}}		
15.0 .25 Submit DDA for Tunnel lighting system	0		10-May-21		13-Jan-22 A	♦ 15.0 25 Subi	mit DDA for Tunr	nel ligh	nting system												1	
15.0 .26 Approval DDA for Tunnel lighting system	0		03-Sep-21		15-Jun-22										♦ 15.0 .2	6 Approval	DDA for Tun	nel lightin	g systen	ļ		
15.4 APS Works for Western Ventilation Building	0	17-Sep-22	17-Sep-22	17-Sep-22	17-Sep-22	 		·												}}	· 	
15.4 .1 Complete site delivery of DeNO2 filters	0		17-Sep-22		17-Sep-22*	,;;;-					; ; ;											♦ 15.4.1
15.4.3 Complete site delivery of electrostatic precipitation system	0		17-Sep-22		17-Sep-22*	<u> </u>																♦ 15.4.3
Page 10 of 24	-			1	1	<u> </u>	1 1 1	- 1	1 1 1	. 1	<u> </u>				<u> </u>	Date	Re	vision	CI	necked	An	proved
Page 10 of 24			2019/0	11 True	nk Doo	d T2 and	Infract	rı ı	cturo M	Jorko					18	3-Dec-19	00V1		WYu			r. 5 7 5 G
Critical Activity		 								VUIKS		PO	IIVOII	EC	\ <u></u>	2-Feb-20	01V0		SPa/		WYu	
◆ ◆ Actual Milestone Actual Work			f	or Dev	/elopm	ents at S	outh A	pro	on			TRAVA	UYGU NUX PUI	BLICS		9-Apr-20 7-Jul-20	01V1 01V2		SPa/ SPa/		WYu WYu	
♦ Baseline Milestone			T I		L - D '	l: D:		/ B	1 OO'							9-Oct-20	01V2		SPa/		WYu	
Baseline Bar			Ihree	e iviont	ns Kol	ling Progr	amme	(1\	/lay-22))						2-Jul-21	02V0		SPa/		WYu	
		ı																				


Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish					. 1		M	A '!		2022									C	
						02	January 09 16		30 06	ebruary 13 20	27	06 13 20 27 03	April 10 17 2	24 01	May 08 15	22 29	9 05	June 12	19 26	July 03 10 17	24 3	August 31 07 14 2	1 28 0	September 4 11	18 25
15.4 .5 Complete site delivery of wash down system	0		17-Sep-22		17-Sep-22*											-								\Q	15.4.5
15.4 .7 Complete site delivery of support system	0		17-Sep-22		17-Sep-22*																			\Q	15.4.7
17.1 Works under Sections 6A, 6C and 12 and Associated Landscape	0	21-Sep-21	04-Oct-21	04-Jun-22	04-Jun-22		-						,								- -				
17.1 .13 Complete footpath 0.25	0		21-Sep-21		04-Jun-22*													1 1	1 1	otpath 0.25					
17.1 .17 Complete street furnitures of at-grade roads 0.25	0		04-Oct-21		04-Jun-22*												17	.1 .17 C	omplete st	eet furnitures	of at-gra	de roads 0.25			
17.4 Remaining Stage 5 Infrastructure Works - Road L10 (Southern Se	0	02-Aug-22	04-Mar-23	04-Jun-22	04-Jun-22		T]				,												
17.4.1 Complete excavation and disposal of material works 0.25	0		17-Feb-23		04-Jun-22												•								
17.4.2 Complete excavation and disposal of material works 0.5	0		04-Mar-23		04-Jun-22*		1 1 1 1 1 1										†								
17.4 .21 Complete drainage installation 0.2	0		18-Oct-22		04-Jun-22*												•								
17.4 .25 Complete manhole for drainage 0.25	0		18-Oct-22		04-Jun-22*												•								
17.4 .31 Complete sewerage installation 0.25	0		02-Aug-22		04-Jun-22*		7		:								•				(• 17.4 .31 Comp	lete sewera	nge install	ation 0.
17.4.35 Complete manhole for sewerage 0.25	0		02-Aug-22		04-Jun-22*								;;;-				•				•	→ 17.4 .35 Comp	lete manho	le for sew	erage (
17.5 Remaining Stage 5 Infrastructure Works - Landscaped Elevated V	85	23-Dec-21	23-Jun-22	13-Apr-22 A	15-Sep-22		† 	;	i-				; <u>;</u> ;-]				. 			- ; -				
17.5 .11 Complete concrete works of pile caps 0.5	0		23-Dec-21		13-Apr-22 A								♦ 17.5.11	1 Complete	! !			. ()							
17.5 .16 Complete concrete works of piers 0.25	0		07-Mar-22		13-May-22 A		T				*	>			◆ 17.5	.16 Con	nplete (concrete	works of p	iers 0.25					
17.5 .12 Complete concrete works of pile caps 0.8	0		08-Jan-22		04-Jun-22	<	>										1 7	.5 .12 C	omplete co	ncrete works	of pile ca	ps 0.8			
17.5.13 Complete concrete works of pile caps 1	0		20-Jan-22		04-Jun-22		<	>					ii-				1 7	.5 .13 C	omplete co	ncrete works	of pile ca	ps 1			
17.5 .17 Complete concrete works of piers 0.5	0		07-Mar-22		04-Jun-22		 				*	>	-				1 7	.5 .17 Co	omplete co	ncrete works	of piers	0.5			
17.5 .18 Complete concrete works of piers 0.8	0		07-Mar-22		04-Jun-22						† · · ·	>					1 7	.5 .18 C	omplete co	ncrete works	of piers	0.8			
17.5 .19 Complete concrete works of piers 1	0		28-Mar-22		25-Jun-22		 				†	→							17. 5	.19 Complete	concrete	works of piers	1		
17.5 .21 Complete concrete works of deck 0.25	0		23-Jun-22		15-Sep-22		 		{- } :		 								♦					• 1	7.5 21 (
17.5.25 Complete prestressing works of deck 0.25	0		23-Jun-22		15-Sep-22	ļ			{- } !		† -								♦		-			♦ 1	7.5 25 (
21.5 Establishment Works for Improvement Works at the Junctions of	72	20-Nov-21	20-Nov-21	13-Apr-22 A	13-Apr-22 A																				
21.5 .3 Complete establishment works for 9 mths completion of softworks	0		20-Nov-21		13-Apr-22 A						†		4 21.5.3	Complete	establish	nent wor	rks for ^c	mths c	ompletion	of softworks					
21.5 .4 Complete whole activities of this cost centre	0		20-Nov-21		13-Apr-22 A		 		{- } 		 		◆ 21.5.4	Complete	whole act	vities of	this co	st centre							
22.1 Pipelines for District Cooling System for Commissioning of AMAV	95	17-Jul-21	16-Nov-21	13-Jan-22 A	11-Jun-22		 				†														
22.1 .3 Complete DCS installation length 0.8	0		17-Jul-21		13-Jan-22 A		♦ 22.	1 .3 Cor	mplete DC	C\$ installatio	nleng	th 0.8													
22.1.5 Complete T&C of DCS system 1	0		16-Nov-21		11-Jun-22		T											22. 1	.5 Comple	e T&C of DCS	Ssystem	1			
22.1 .6 Complete whole activities of this cost centre 1	0		16-Nov-21		11-Jun-22		 						;;-					22.1	.6 Comple	e whole activi	ities of th	is cost centre 1			
34.2 Common Utilities Enclosure (CUE) under Section 13 of the Works	72	06-Apr-22	21-Nov-22	08-Jun-22	02-Sep-22		† ! !	{	i- -		†		i i i -					·							
34.2 .2 Complete excavation of CUE	0		24-Aug-22		08-Jun-22												•						> 34.2.20	Complete	excavati
34.2.4 Complete concrete works of base slab of CUE 0.5	0		06-Apr-22		11-Jun-22		1 1 1 1 1 1					♦					•	♦ 34.2	.4 Comple	e concrete wa	orks of b	ase slab of CUE	0.5		
34.2.8 Complete concrete works of walls of CUE 0.5	0		06-Apr-22		11-Jun-22							•	,			:		♦ 34.2	.8 Comple	e concrete wo	orks of w	alls of CUE 0.5			
34.2 .12 Complete concrete works of top slab of CUE 0.5	0		06-Apr-22		11-Jun-22							\Q						♦ 34.2	.12 Compl	ete concrete v	works of 1	op slab of CUE	0.5		
34.2.5 Complete concrete works of base slab of CUE 0.75	0		21-Nov-22		02-Sep-22		-						, , -										•		
34.2.9 Complete concrete works of walls of CUE 0.75	0		21-Nov-22		02-Sep-22		; ;		i-		† 	;;;	; ; ; -								- ; ; -				
34.2 .13 Complete concrete works of top slab of CUE 0.75	0		21-Nov-22		02-Sep-22		i i		i-		<u> </u>												•		
35 Services Gallery	97	08-Oct-21	14-Jun-22	13-Apr-22 A	28-Sep-22				i-				ii												
35.16 Complete 20% of total length (measured on plan) of SG structures in Drill-and-Break and Drill-and-Blast Tunnel	0		04-Feb-22		13-Apr-22 A			,	\rightarrow				◆ 35.16 C	Complete 2	0% of tota	I length	(meası	red on I	olan) of SC	structures in	Drill-and	l-Break and Drill-	and-Blast T	Tunnel	
35.32 Complete 50% of total volume (measured on plan) of excavation for Lower Basement of East Ventilation Building	0		29-Nov-21		13-Apr-22 A		-						◆ 35.32 C	Complete 5	0% of tota	l volume	e (meas	sured on	plan) of e	cavation for l	Lower Ba	sement of East	entilation l	Building	
35.9 Approval of DDA submission for Services Gallery E&M design by the SO	0		08-Oct-21		04-Jun-22*		;; !						; <u>;</u> <u>;</u> -				3 5	.9 Appro	val of DDA	submission f	for Servi	es Gallery E&M	design by t	he SO	
· · · · · · · · · · · · · · · · · · ·	ļ					<u>'</u>		1 1	' '	1 1					1 1	1	-				- 4			1 1	
Page 11 of 24				—															D 18-De	ate -19 00	Revisi	on Che WYu	cked	Appro	ved
Data Date: 04-Jun-22		ED/2	2018/C)4 Trur	ik Roa	ad '	Т2 а	anc	d Inf	rastr	uct	ture Works	S /						22-Fel		V0	SPa/LL	o	NYu	
♦ Actual Milestone			f	or Dev	elopn/	ner	nts a	at S	Sout	aA d	ror	า		B	OUY AVAUX	GUE	S		09-Ap	-20 01	V1	SPa/LL	o V	۷Yu	
Actual Work					•					•				IK	AUAVA	PUDL			17-Jul- 09-Oc		V2 V3	SPa/LL SPa/LL		NYu NYu	
Baseline Bar			Three	Month	ns Ro	llin	g Pi	rog	ıram	ıme ((Ma	ay-22)							09-Oc		V3 2V0	SPa/LL SPa/LL		WYu WYu	
									•		`	,										1			

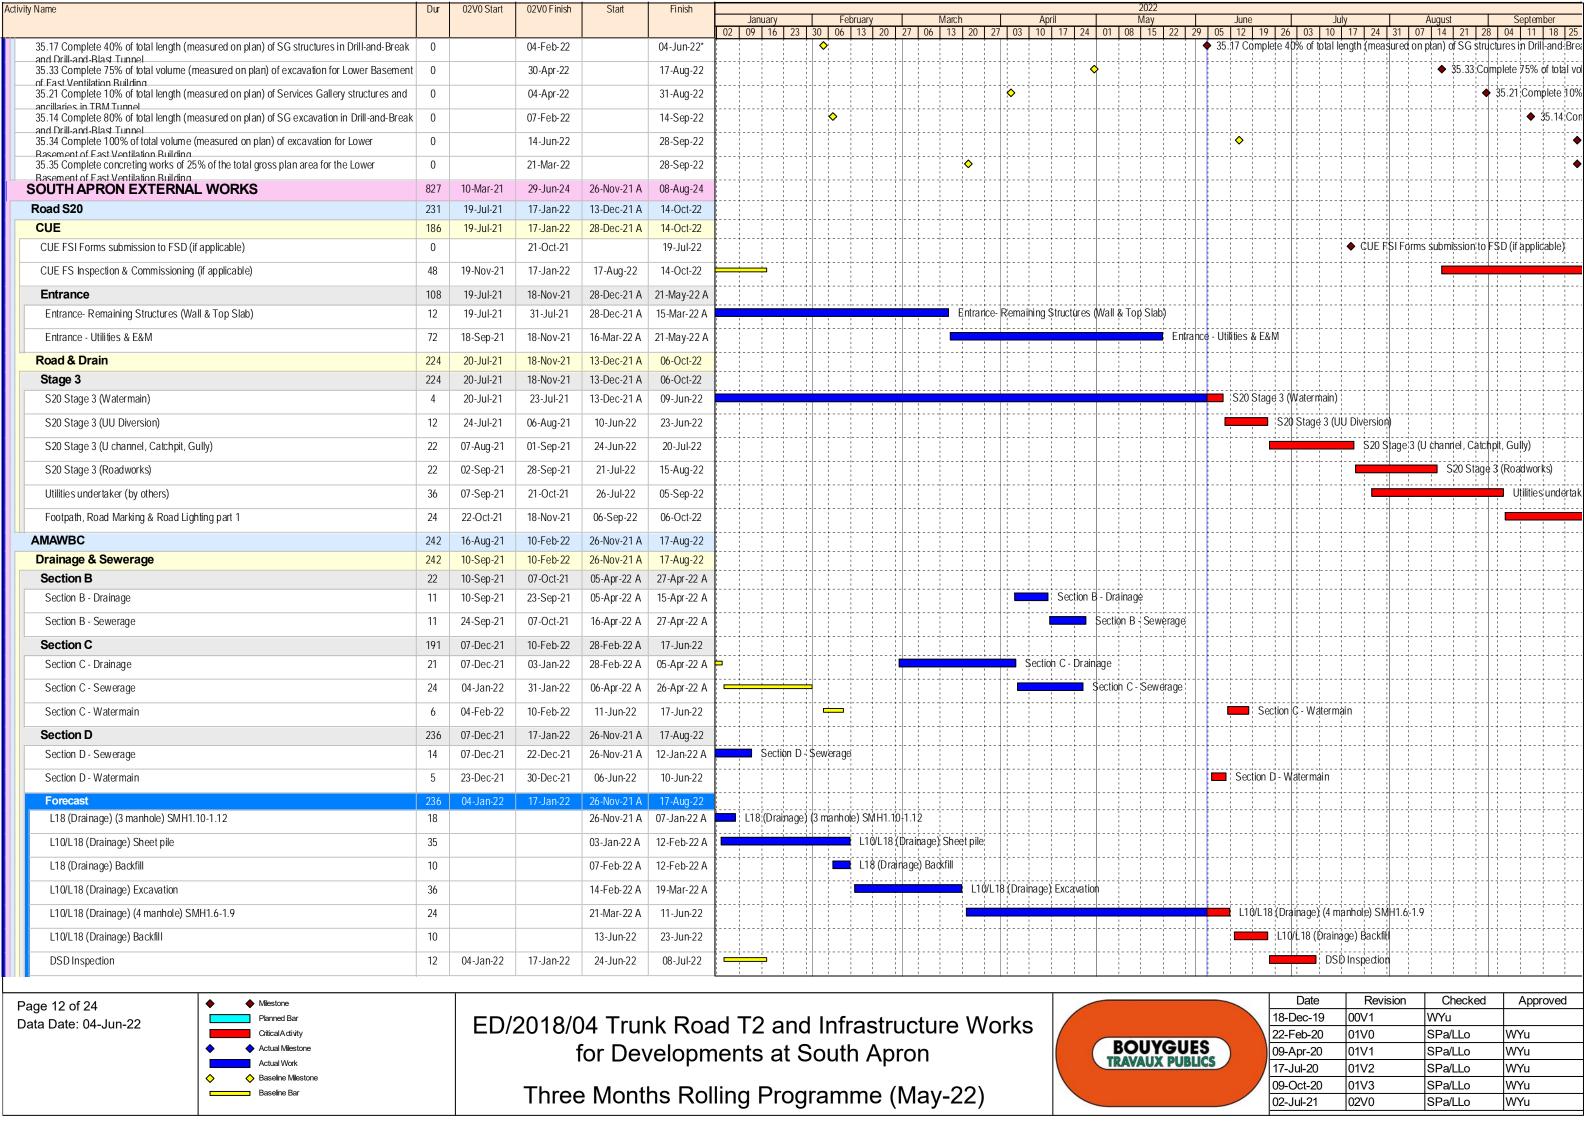


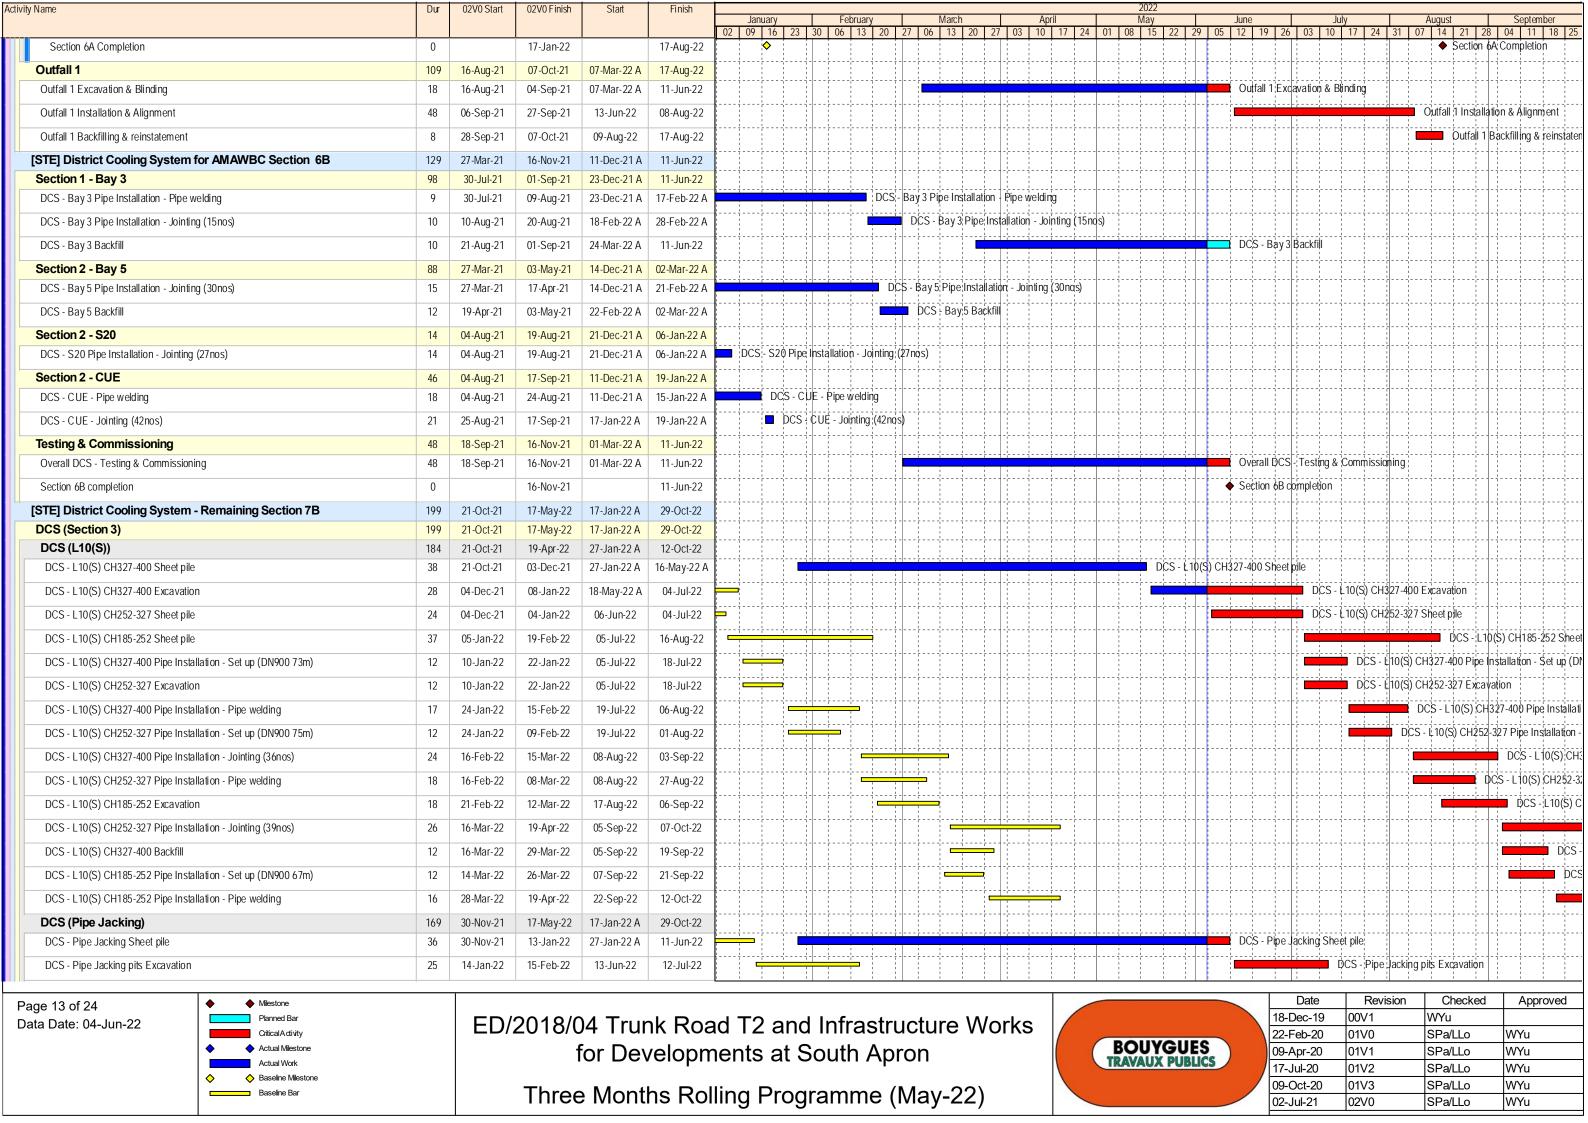


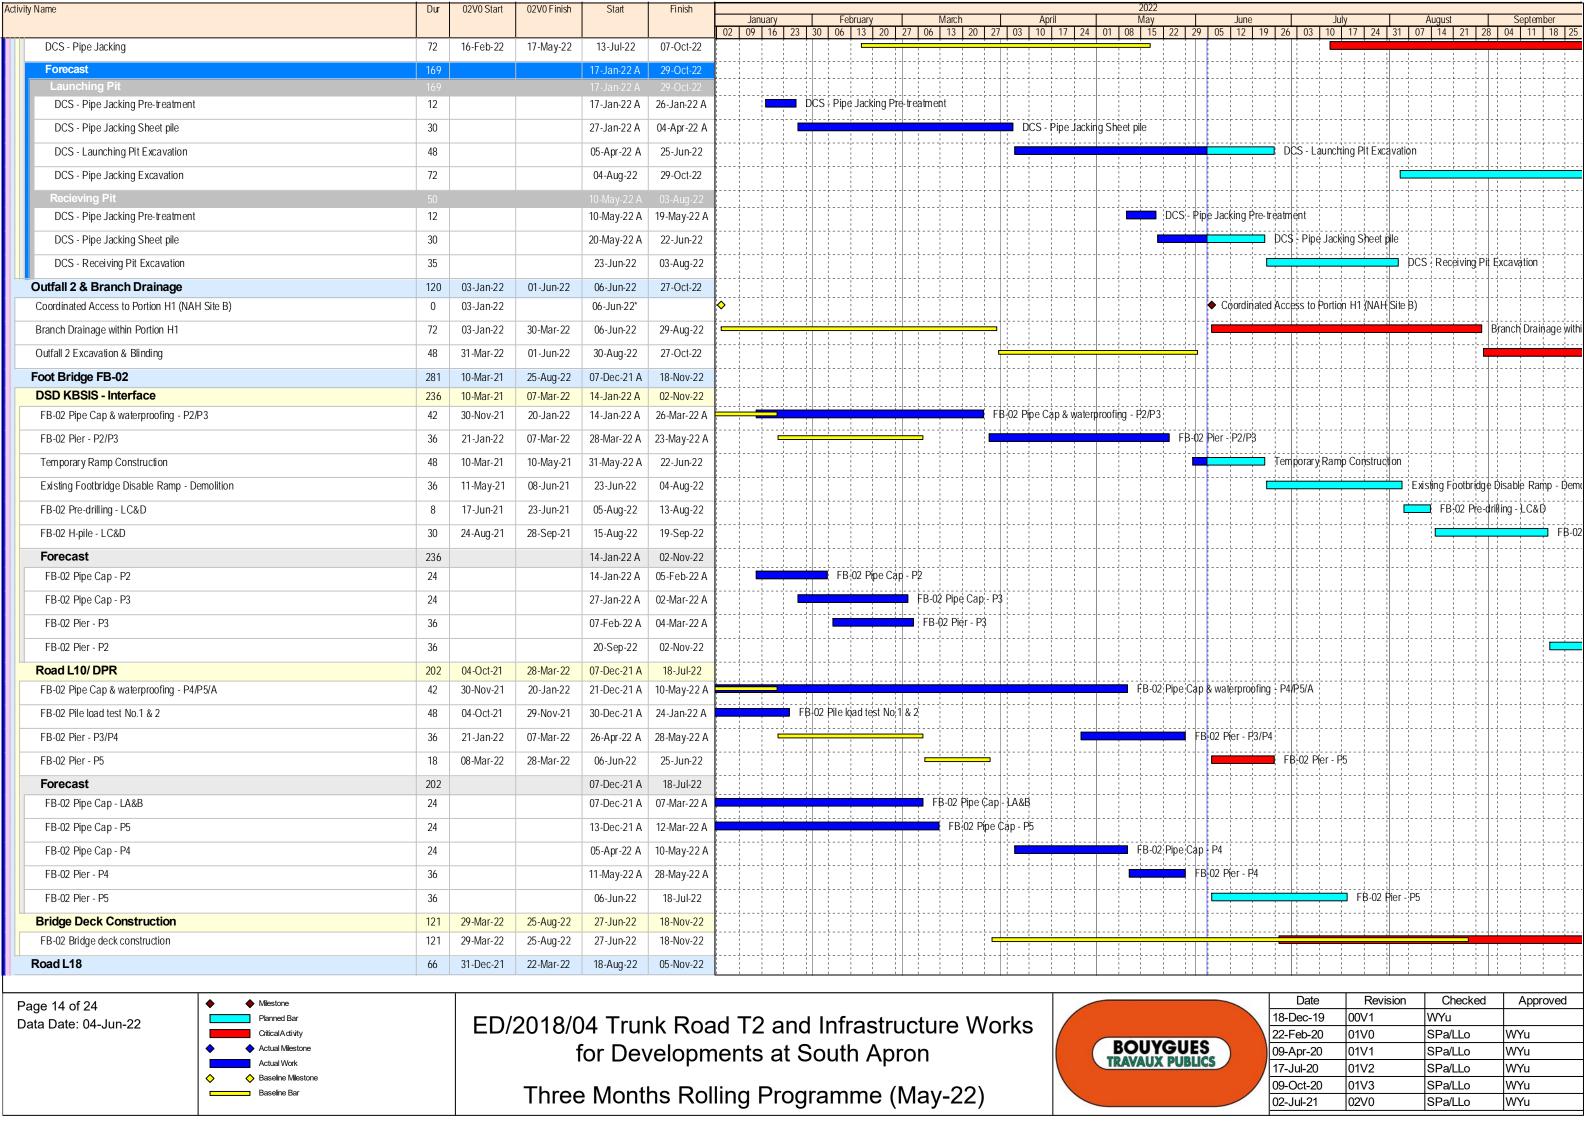


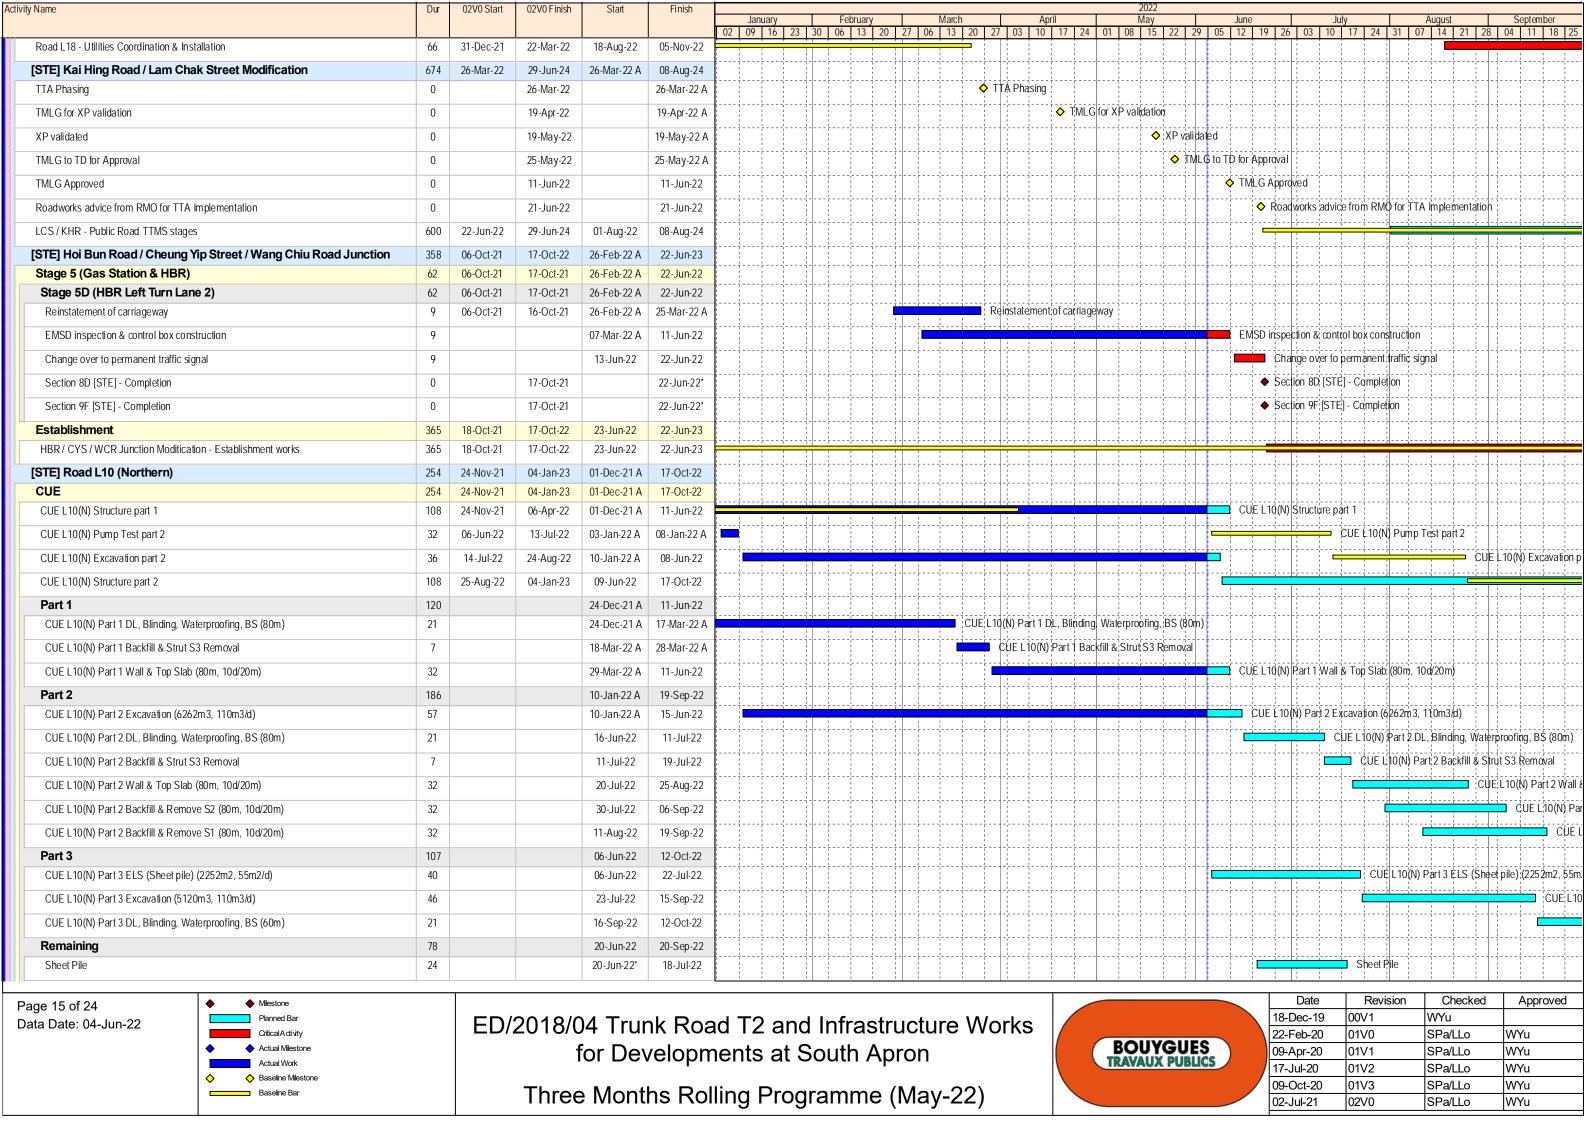

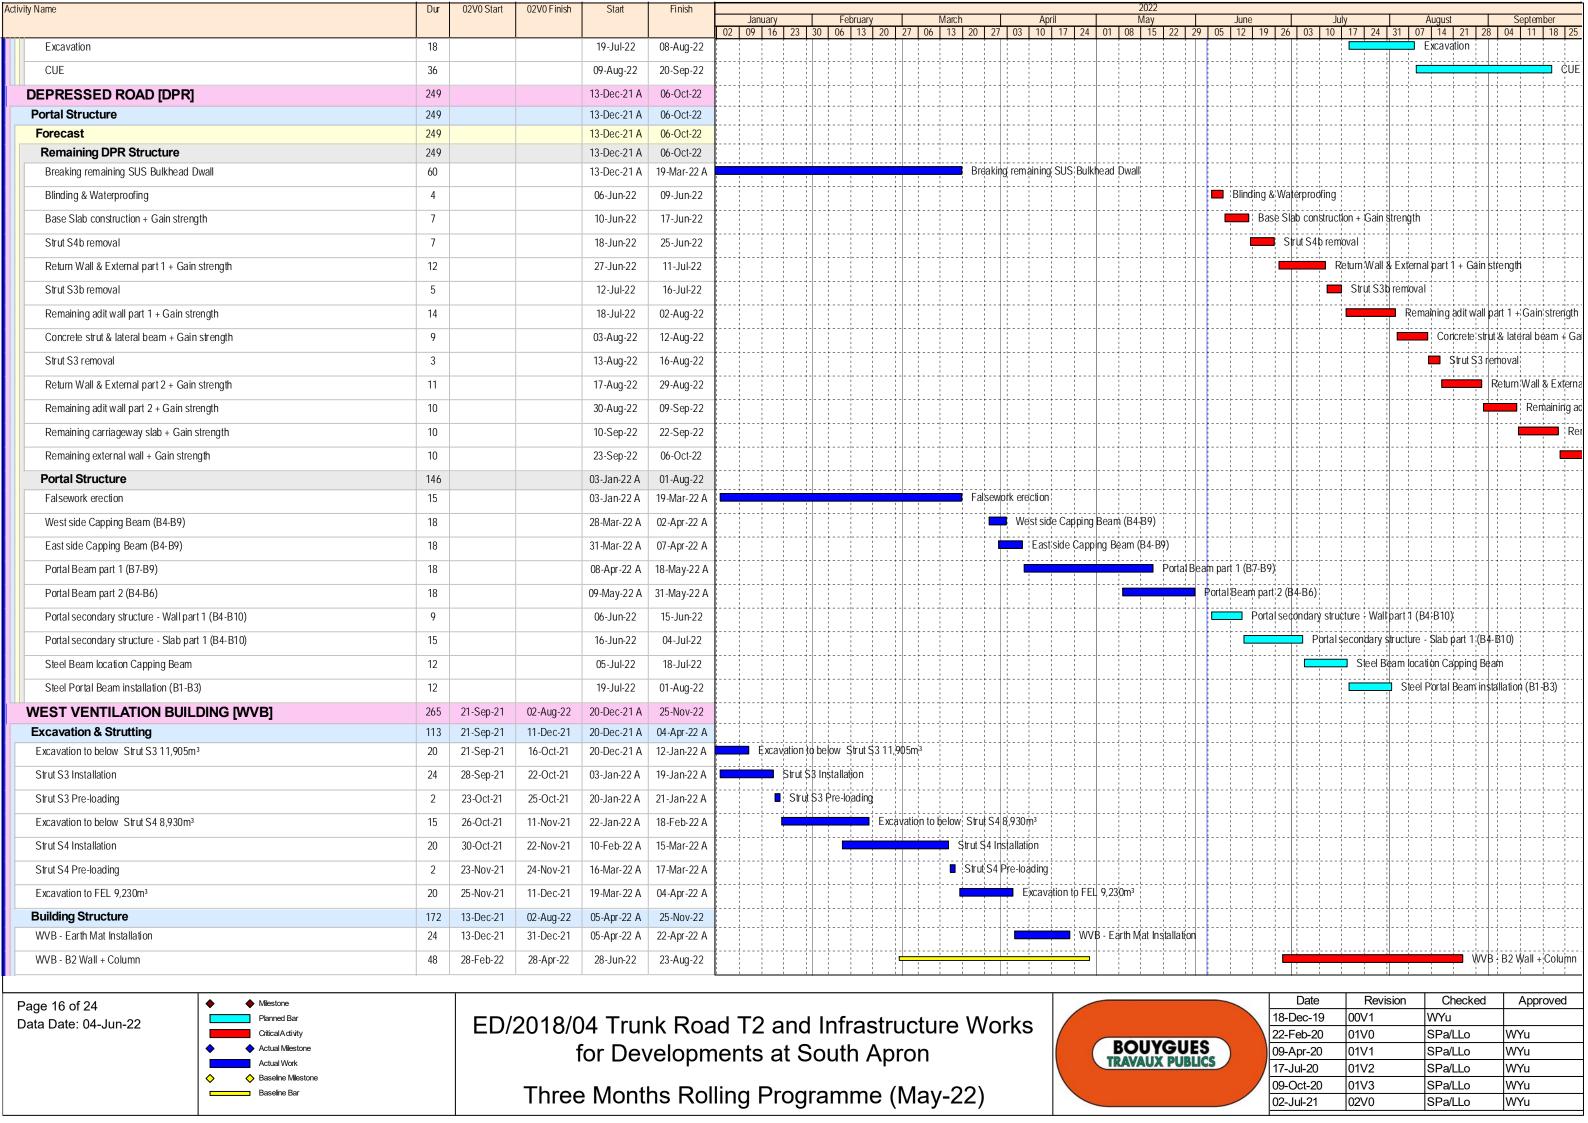

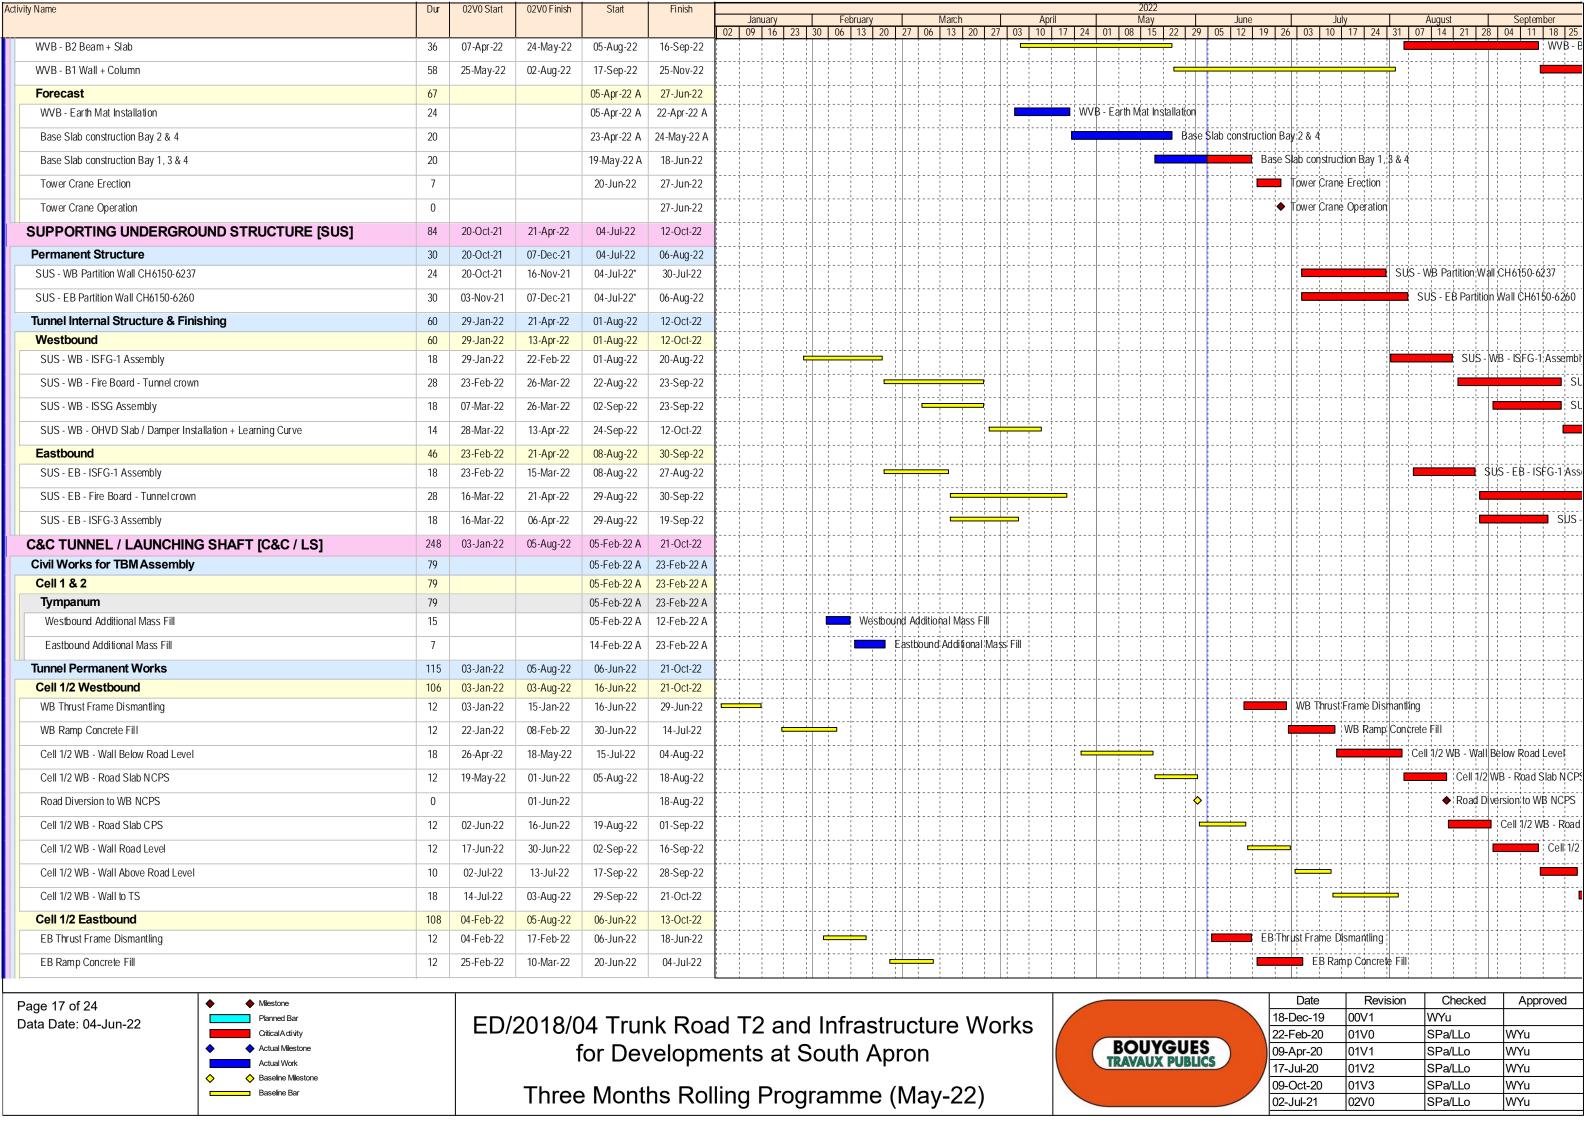


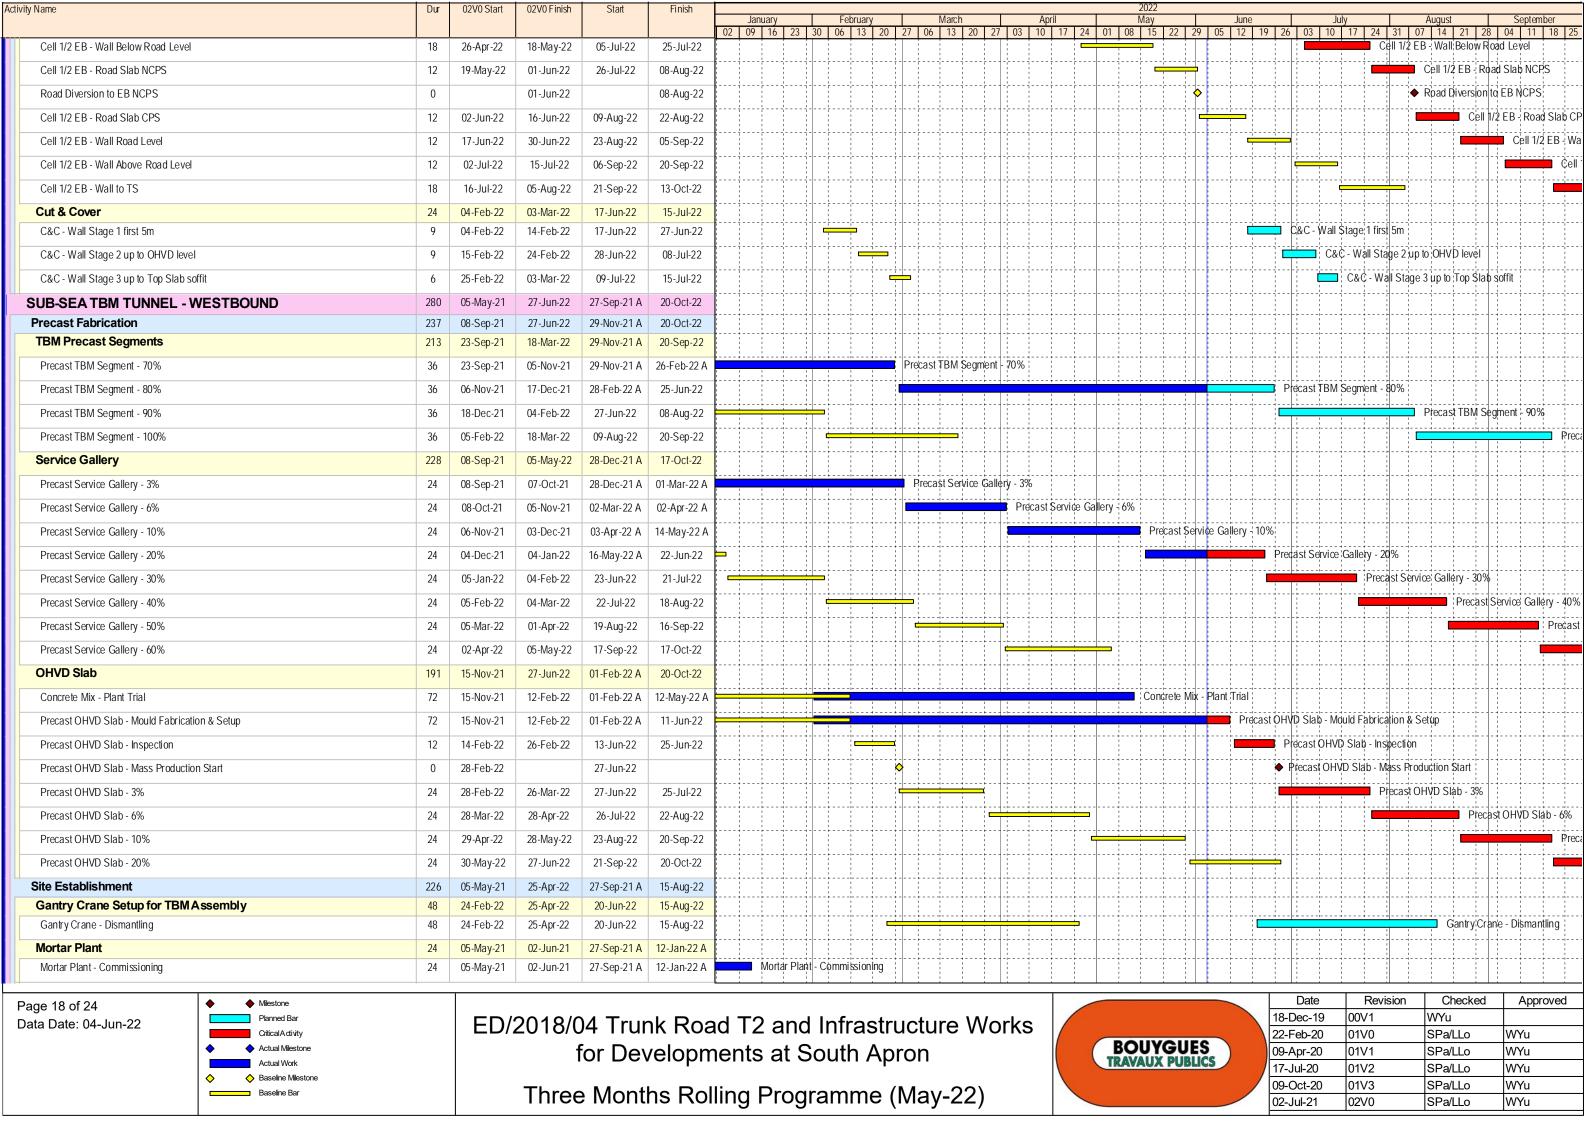


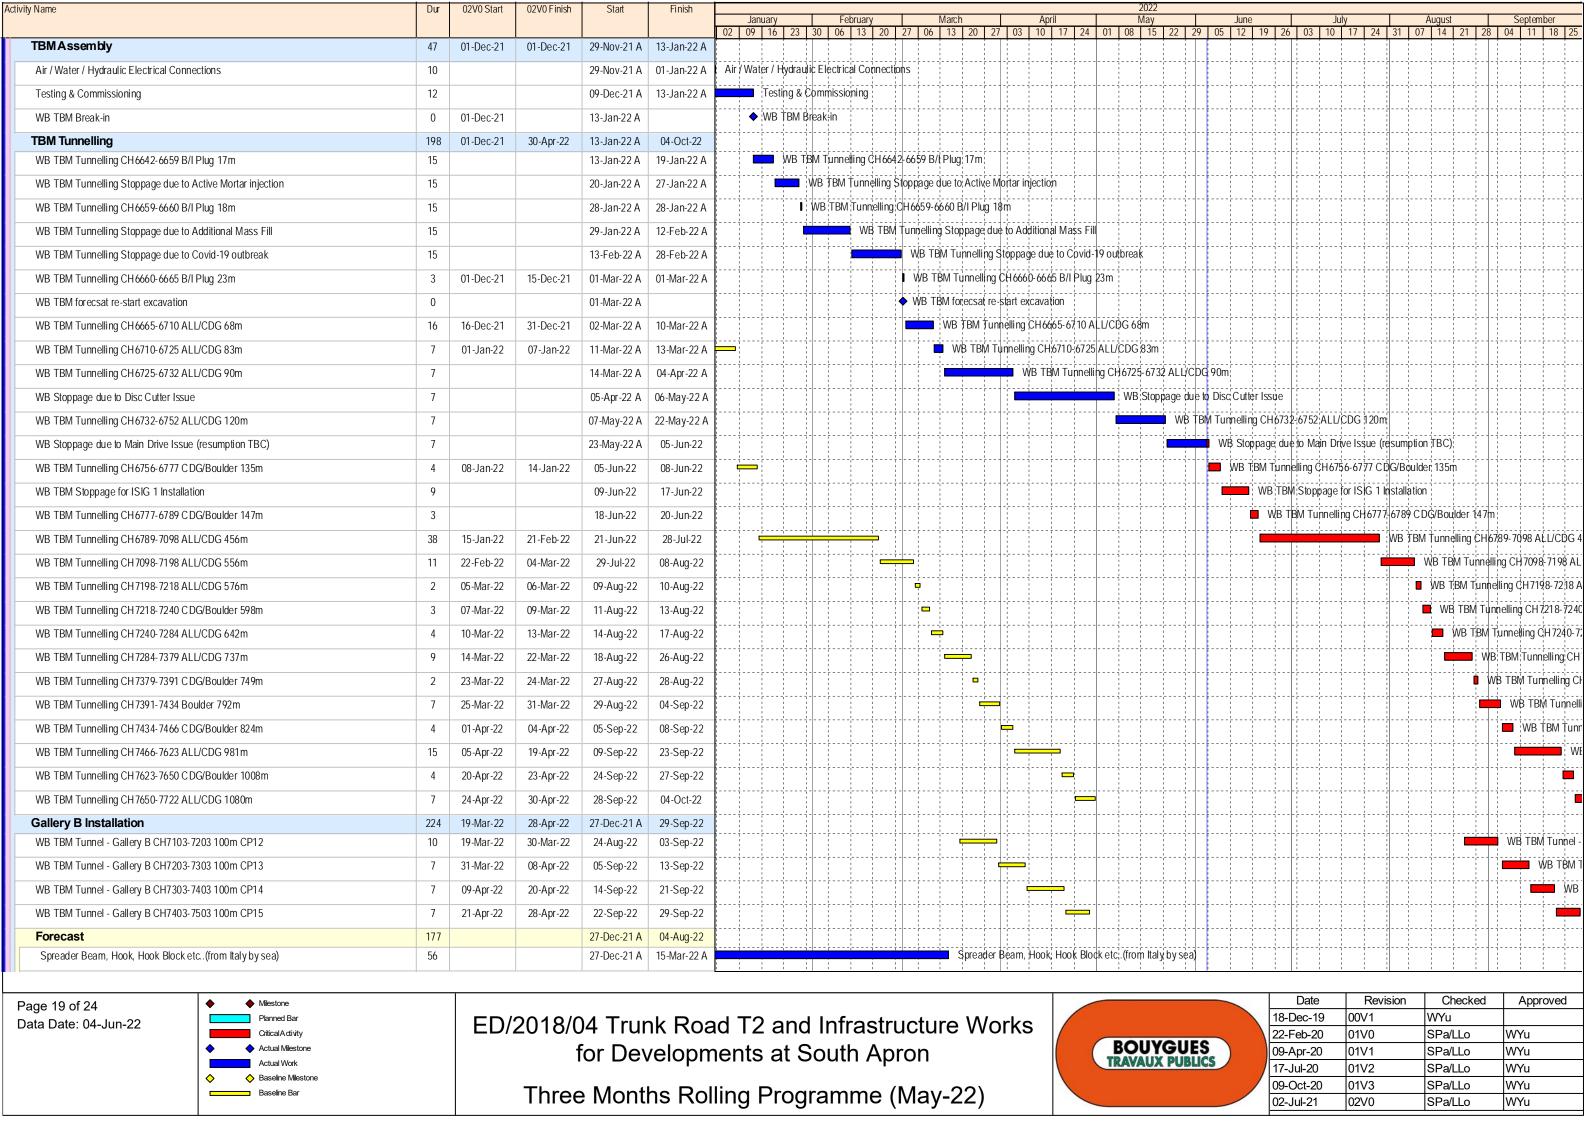


Activity Name Dur	02V0 Start	02V0 Finish	Start	Finish	2022 January February March April May June July August September	
					02 09 16 23 30 06 13 20 27 06 13 20 27 06 13 20 27 08 10 17 24 01 08 15 22 29 05 12 19 26 03 10 17 24 31 07 14 21 28 04 11 18 25	
Wheels (from Italy by air) 10					Wheels (from Italy by air)	
Ramp delivery (from China by road) 6				11-Jan-22 A		
Loader (from China by road) 13			21-Jan-22 A		Loader (from China by road)	
Ramp pre-assembly at surface 12			27-Jan-22 A	16-Feb-22 A	Ramp pre-assembly at surface	
Loader pre-assembly at surface 6			17-Feb-22 A	25-Feb-22 A	Loader pte-assembly at surface	
Shifting way curve shape extension & Footing 6			06-Jun-22	11-Jun-22	Shifting way curve shape extension & Fopting	
Construction of Notch/Mass Fill to C&C Road Level 9			13-Jun-22	22-Jun-22	Construction of Notch/Mass Fill to C&C Road Level	
Lower ISIG into Shaft 3			13-Jun-22	15-Jun-22	■ Lower ISIG into Shaft:	
Thrust Frame Removal 6			16-Jun-22	22-Jun-22	Thrust Frame Removal	
Install abd Assembly of Spreader Beam 6			16-Jun-22	22-Jun-22	Install abd Assembly of Spreader Beam	
ISIG Commissioning 6			23-Jun-22	29-Jun-22	ISIG Commissioning	
Gallery G-W1 to W5 by crawler crane @ 1 no/d 2			30-Jun-22	02-Jul-22	Gallery G-W1 to W5 by crawler crane @ 1 no/d	
WB ISIG Gallery B Installation start 0			30-Jun-22		◆ WB I\$IG Gallery B Installation start	
Gallery EMVD installation by crawler crane 1			04-Jul-22	04-Jul-22	■ Gallery, EMVD installation by crawler crane	
Gallery G-W6 to G-W12 installation by ISIG @ 3nos/d 2			05-Jul-22	06-Jul-22	■ Gallery G-W6 to G-W12 installation by ISIG @ 3nos/d	
Gallery B installation inside FT @ 6nos/d 1			07 -Jul-22	07-Jul-22	■ Gallery B installation inside FT @ 6nqs/d	
Steel Bridge Installation 1			08-Jul-22	08-Jul-22	■ Steel Bridge Installation	
WB Sub-sea Galery B Installation started 0			09-Jul-22		◆ WB Sub-sea Galery, B Installation started:	
WB Gallery B CH6642-6742 100m @4nos/day 13			09-Jul-22	23-Jul-22	WB Gallery B CH6642-6742 100m @4nos/day,	
WB Gallery B CH6742-6855 113m @6nos/day 10			25-Jul-22	04-Aug-22	WB Gallery B CH6742-6855 113m @6no	
SUB-SEA TBM TUNNEL - EASTBOUND 247	03-Jan-22	30-May-22	14-Dec-21 A		▋╌╌┆╌╌┆╌╌┆╌╌┆╌╌┆╌╌┆╌╌┆╌╌┆╌╌┆╌╌┆╌╌┆╌╌┆╌╌┆	
TBM Assembly 110			14-Dec-21 A			
Lifting & Welding of Tailskin to Shield 28			14-Dec-21 A	06-Jan-22 A	Lifting & Welding of Tailskin to Shield	
Air / Water / Hydraulic Electrical Connections 10			20-Dec-21 A	06-Jan-22 A	Air / Water / Hydraulic Electrical Connections	
Testing & Commissioning 12			26-Dec-21 A	10-Mar-22 A	Testing & Commissioning	
Thrust Frame Installation 10			30-Dec-21 A	06-Jan-22 A	Thrust Frame Installation	
Power On 1			07-Jan-22 A	07-Jan-22 A	■ Power On	
WB TBM Tunnelling Stoppage due to Additional Mass Fill 15			14-Feb-22 A	23-Feb-22 A	WB TBM Tunnelling Stoppage due to Additional Mass/Fill	
S1282 EB TBM Break-in 0				10-Mar-22 A	◆ S1282 EB TBM Break-in	
TBM Tunnelling 173	03-Jan-22	22-May-22	11-Mar-22 A	08-Oct-22		
EB TBM Tunnelling CH6640-6665 B/I Plug 25m 16	03-Jan-22	18-Jan-22	11-Mar-22 A	25-Mar-22 A	EB TBM Tunnelling CH6640-6665 B/I Plug 25m	
EB TBM Tunnelling CH6665-6710 ALL/CDG 70m 15	19-Jan-22	02-Feb-22	26-Mar-22 A	02-Apr-22 A	EB TBM Tunnelling CH6665-6710 ALL/CDG 70m	
EB TBM Tunnelling CH6710-6756 ALL/CDG 116m 7	03-Feb-22	09-Feb-22	03-Apr-22 A	27-Apr-22 A	EB TBM Tunnelling CH6710-6756 ALL//CDG 116m	
EB TBM Tunnelling CH6756-6777 CDG/Boulder 135m 4	10-Feb-22	16-Feb-22	28-Apr-22 A	04-May-22 A	EB TBM Tunnelling CH6756-6777 CDG/Boulder 135m	
WB TBM Stoppage for ISIG 1 Installation 9			06-May-22 A	12-May-22 A	WB TBM Stoppage for ISIG 1 Installation	
EB TBM Tunnelling CH6777-6789 CDG/Boulder 149m 3			13-May-22 A	21-May-22 A	EB.TBM/Tunn/elling/ CH6777-6789 CDG/Boulder 149m	
EB TBM Tunnelling CH6789-7098 ALL/CDG 458m 38	17-Feb-22	26-Mar-22	22-May-22 A		EB TBM Tunnelling CH6789-7098 ALL/CDG 458m	
EB TBM Tunnelling CH7098-7198 ALL/CDG 558m 11	27-Mar-22	06-Apr-22	04-Jul-22	14-Jul-22	EB TBM Tunnelling CH7098-7198 ALLI/CDG 558m	
EB TBM Tunnelling CH7198-7218 ALL/CDG 578m 2	07-Apr-22	08-Apr-22	15-Jul-22	16-Jul-22	■ EB:TBM:Tunnelling: CH7:198-7:218 ALL/CDG 578m	
EB TBM Tunnelling CH7218-7240 CDG/Boulder 600m 3	09-Apr-22	11-Apr-22	17-Jul-22	19-Jul-22	■ EB TBM Tunnelling CH7218-7240 CDG/Boulder 600n	
3						
Page 20 of 24 ♦ Milestone					Date Revision Checked Approved	
Data Date: 04-Jun-22	ad T2 and Infrastructure Works					
CriticalActivty ♦ Actual Milestone					22-Feb-20 OTVO SPA/LLO WYU	
Actual Work	Actual Work TOT DC V CTOPTHICTES AT COUNTY TRAVAUX PUBLICS					
♦ Baseline Milestone Baseline Bar		Three	Mont	he Ral	Iling Programme (May-22)	
		111166	, IVIOIIL		ming Programme (way-22)	

Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	January February Mai	ch I April	2022 May	June	T hu	lv	I Au	ust I	Septem	her
ED TDM Turns allies CH72 40 7204 NH/CDC 444	4	12 A == 22	15 A 22	20 1.1.22	22 1 22	2 09 16 23 30 06 13 20 27 06 1			29 05 12 19	26 03 10			4 21 28	04 11	18 25
EB TBM Tunnelling CH7240-7284 ALL/CDG 644m	4	12-Apr-22	15-Apr-22	20-Jul-22	23-Jul-22						1		ing CH7240-	1	
EB TBM Tunnelling CH7284-7379 ALL/CDG 739m	9	16-Apr-22	24-Apr-22	24-Jul-22	01-Aug-22								Tunnelling Cl	1	
EB TBM Tunnelling CH7379-7391 CDG/Boulder 751m	2	25-Apr-22	26-Apr-22	02-Aug-22	03-Aug-22								Tunnelling (1 1	
EB TBM Tunnelling CH7391-7434 Boulder 794m 7		27-Apr-22	03-May-22	04-Aug-22	10-Aug-22			T				E	3 TBM Tunne	1	
EB TBM Tunnelling CH7434-7466 CDG/Boulder 826m 4		04-May-22	07-May-22	09-Sep-22	12-Sep-22						; ; ;			= E	B TBM Tu
EB TBM Tunnelling CH7466-7623 ALL/CDG 983m		08-May-22	22-May-22	24-Sep-22	08-Oct-22										
Gallery B Installation	213	21-Apr-22	30-May-22	28-Jan-22 A	·							 <u></u>		ļ	
EB TBM Tunnel - Gallery B CH7103-7203 100m CP12	9	21-Apr-22	30-Apr-22	10-Aug-22	19-Aug-22								EB TBM	11	
EB TBM Tunnel - Gallery B CH7203-7303 100m CP13	8	03-May-22	12-May-22	20-Aug-22	29-Aug-22							<u> </u> -	<u>ا</u> ا	B TBM Tur	
EB TBM Tunnel - Gallery B CH7303-7403 100m CP14	8	13-May-22	21-May-22	30-Aug-22	07-Sep-22									EBTI	
EB TBM Tunnel - Gallery B CH7403-7503 100m CP15	7	23-May-22	30-May-22	08-Sep-22	16-Sep-22										EB TBM
Forecast	182			28-Jan-22 A								 -		ļļ	
Spreader Beam, Hook, Hook Block etc(from Italy by sea)	56				05-Mar-22 A		der Beam, Hook, Hook Block et	tc(Irom Italy by sea)							<u> </u>
Front Ramp (from China by road)	9				19-Feb-22 A	Front Ramp (fron					-			<u> </u>	
Mild and Rear Ramp + Loader (from China by road)	9				22-Feb-22 A	Mild and Rear	Ramp + Loader (from China by								
Ramp pre-assembly at surface	24				25-Apr-22 A			Ramp pre-assembly at su							
Shifting way curve shape extension & Footing	6				04-May-22 A				shape extension & I	Footing				<u> </u>	
Loader pre-asembly	10			26-Apr-22 A	04-May-22 A			Loader pre-asemb							
Construction of Notch/Mass Fill to C&C Road Level	9			05-May-22 A	12-May-22 A				n of Notch/Mass Fill t	o C&C Road Le	vel				
Lower ISIG into Shaft	3			05-May-22 A	12-May-22 A			Lower ISIG	into Shaft						
Thrust Frame Removal (TBC)	6			13-May-22 A	19-May-22 A			Thrust	Frame Removal (TE	BC)					
Install and Assembly of Spreader beam etc				13-May-22 A	23-May-22 A			Ins	tall and Assembly of	Spreader beam	etc				
Gallery G-E1 to E5 by αawler crane @ 1 no/d	2			23-May-22 A	26-May-22 A			1 1 1 1	Gallery G-E1 to E5 by	1 1	@ 1 no/d				
ISIG Commissioning	6			24-May-22 A	30-May-22 A				ISIG Commissioni	ng					
Gallery EMVD installation by crawler	1			27-May-22 A	27-May-22 A			<u>-</u>	Gallery EMVD install	ation by crawler	-				
EB ISIG Gallery B Installation start	0			31-May-22 A					EB ISIG Gallery B	Installation star	t			 	
Gallery G-E6 to G-E12 installation by ISIG @ 3nos/d	3			31-May-22 A	04-Jun-22 A				Gallery G-E6 to	o G-E12 installa	tion by ISK	@ 3nos/d			
Steel Bridge Installation	1			05-Jun-22	05-Jun-22				Steel Bridge I	nstallation					
Gallery B installation inside FT @ 6nos/d	3			06-Jun-22	08-Jun-22				■ Gallery B in	stallation inside	FT @ 6no	s/d			
EB Gallery B CH6642-6742 100m @4nos/day	11			09-Jun-22	19-Jun-22				EB	Gallery B CH66	642-6742 1	00m @4nos	day		
EB Gallery B CH6742-6855 113m @6nos/day	7			20-Jun-22	26-Jun-22					I EB Gallery B	CH6742-68	55 1 13m @	6nos/day		
SUB-SEA TUNNEL CROSS PASSAGE (CP7-CP27a/b)	244	31-Jul-21	28-Dec-22	10-May-21 A	22-Oct-22								}		
CP TBM Design / Fabrication / FAT / Delivery	144	31-Jul-21	22-Mar-22	,	19-Mar-22 A						1				
Fabrication / Refurbishment	144	31-Jul-21	21-Jan-22	10-May-21 A	10-Feb-22 A	Fabrication / Refurbishm	ent				1 1 1 1			1 1 1 1 1 1	
FAT	24	22-Jan-22	22-Feb-22	11-Feb-22 A	28-Feb-22 A	FAT									
Delivery of TBM components to the Site	24	23-Feb-22	22-Mar-22	01-Mar-22 A	19-Mar-22 A		Delivery of TBM compon	nents to the Site						1	
CP Precast Lining Fabrication	188	23-Feb-22	28-Dec-22	17-Dec-21 A	13-Oct-22									1 1	
CP Precast Lining Segment - 3%	18	23-Feb-22	15-Mar-22	17-Dec-21 A	15-Jan-22 A		CP Precast Lining Segment -	3%							
CP Precast Lining Segment - 6%	18	16-Mar-22	06-Apr-22	17-Jan-22 A	29-Jan-22 A		CP Precast L	ining Segment - 6%			!				
CP Precast Lining Segment - 10%	24	07-Apr-22	10-May-22	31-Jan-22 A	19-Feb-22 A			CP Precast L	ining Segment - 10%)					
CP Precast Lining Segment - 20%	24	11-May-22	08-Jun-22	21-Feb-22 A	30-Mar-22 A				CP Precast	Lining Segmen	t - 20%			1 1 1 1 1 1	
Page 21 of 24		1									Revi	sion	Checked	Appr	oved
Data Date: 04-Jun-22	ate: 04-Jun-22 Planned Bar FD/2018/04 Trunk Road T2 and Infrastructure Works								_	8-Dec-19	00V1		Yu		
CriticalAditity ♦ Actual Milestone		for Developments at South Apron Three Months Rolling Programme (May-22)							22-Feb-20 9-Apr-20	01V0 01V1		Pa/LLo Pa/LLo	WYu WYu		
Actual Work										01V1		Pa/LLo	WYu		
♦ Baseline Milestone Baseline Bar									9-Oct-20	01V3		Pa/LLo	WYu		
	The strength of the strength o)2-Jul-21	02V0	SI	Pa/LLo	WYu		

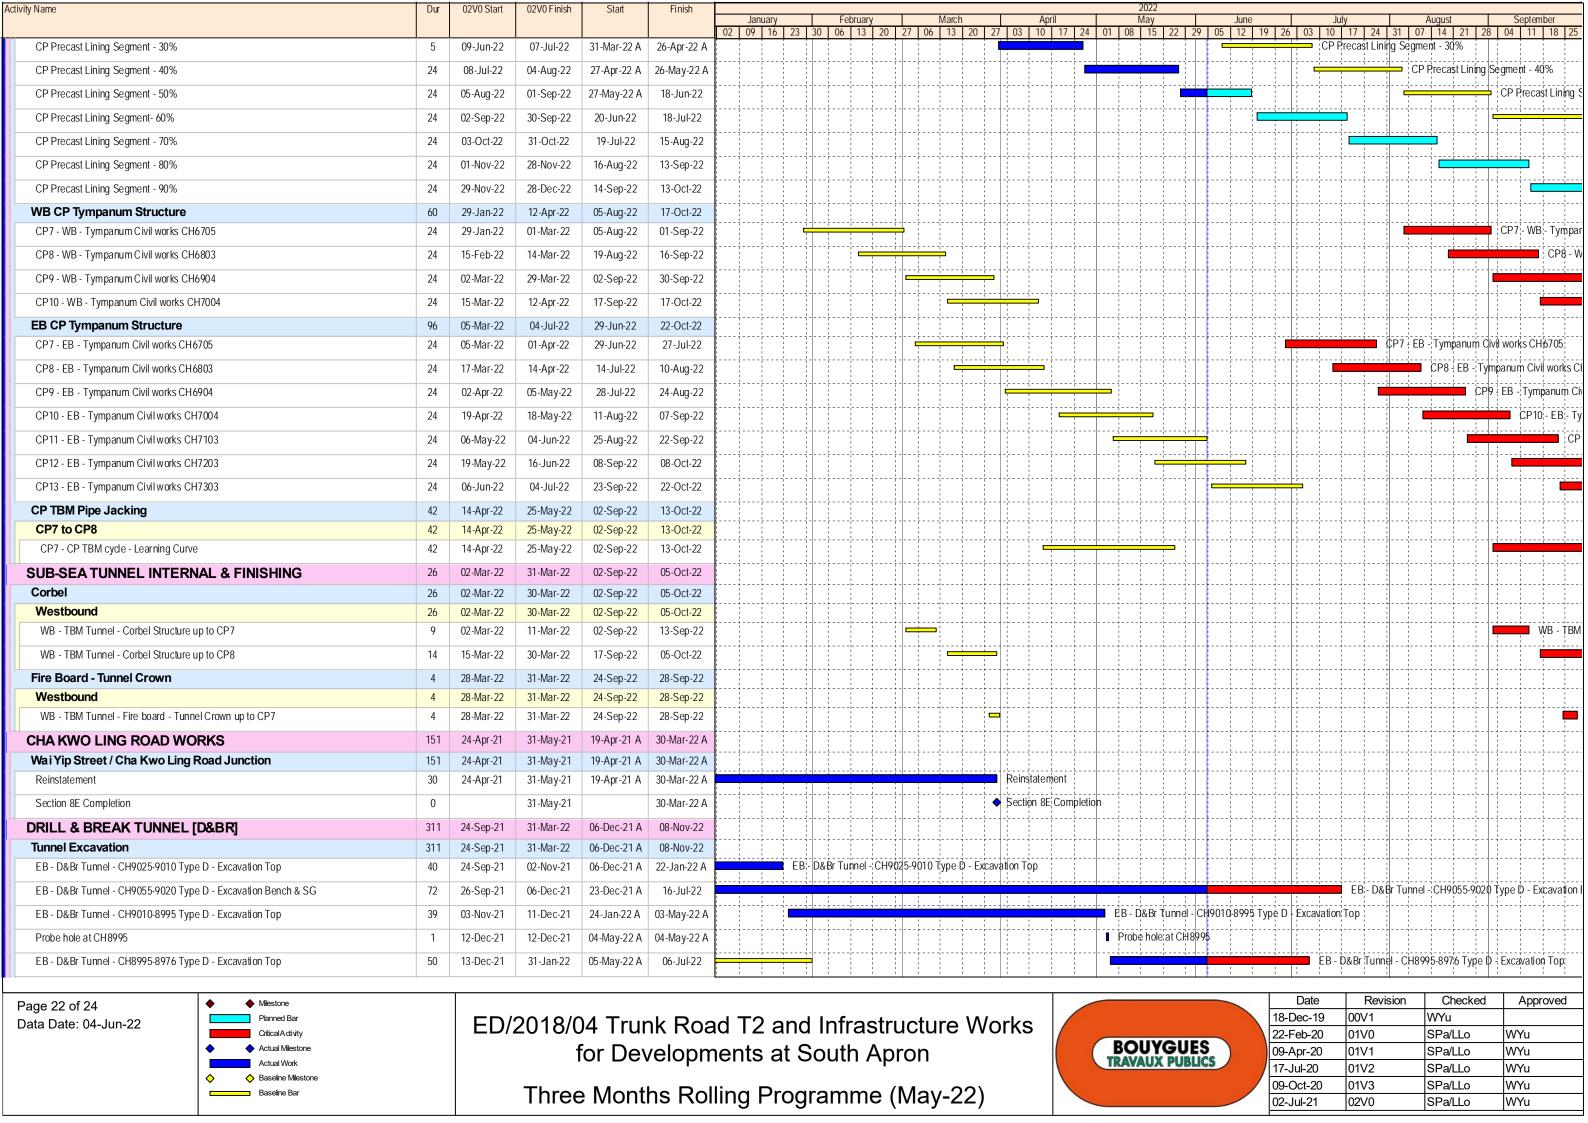

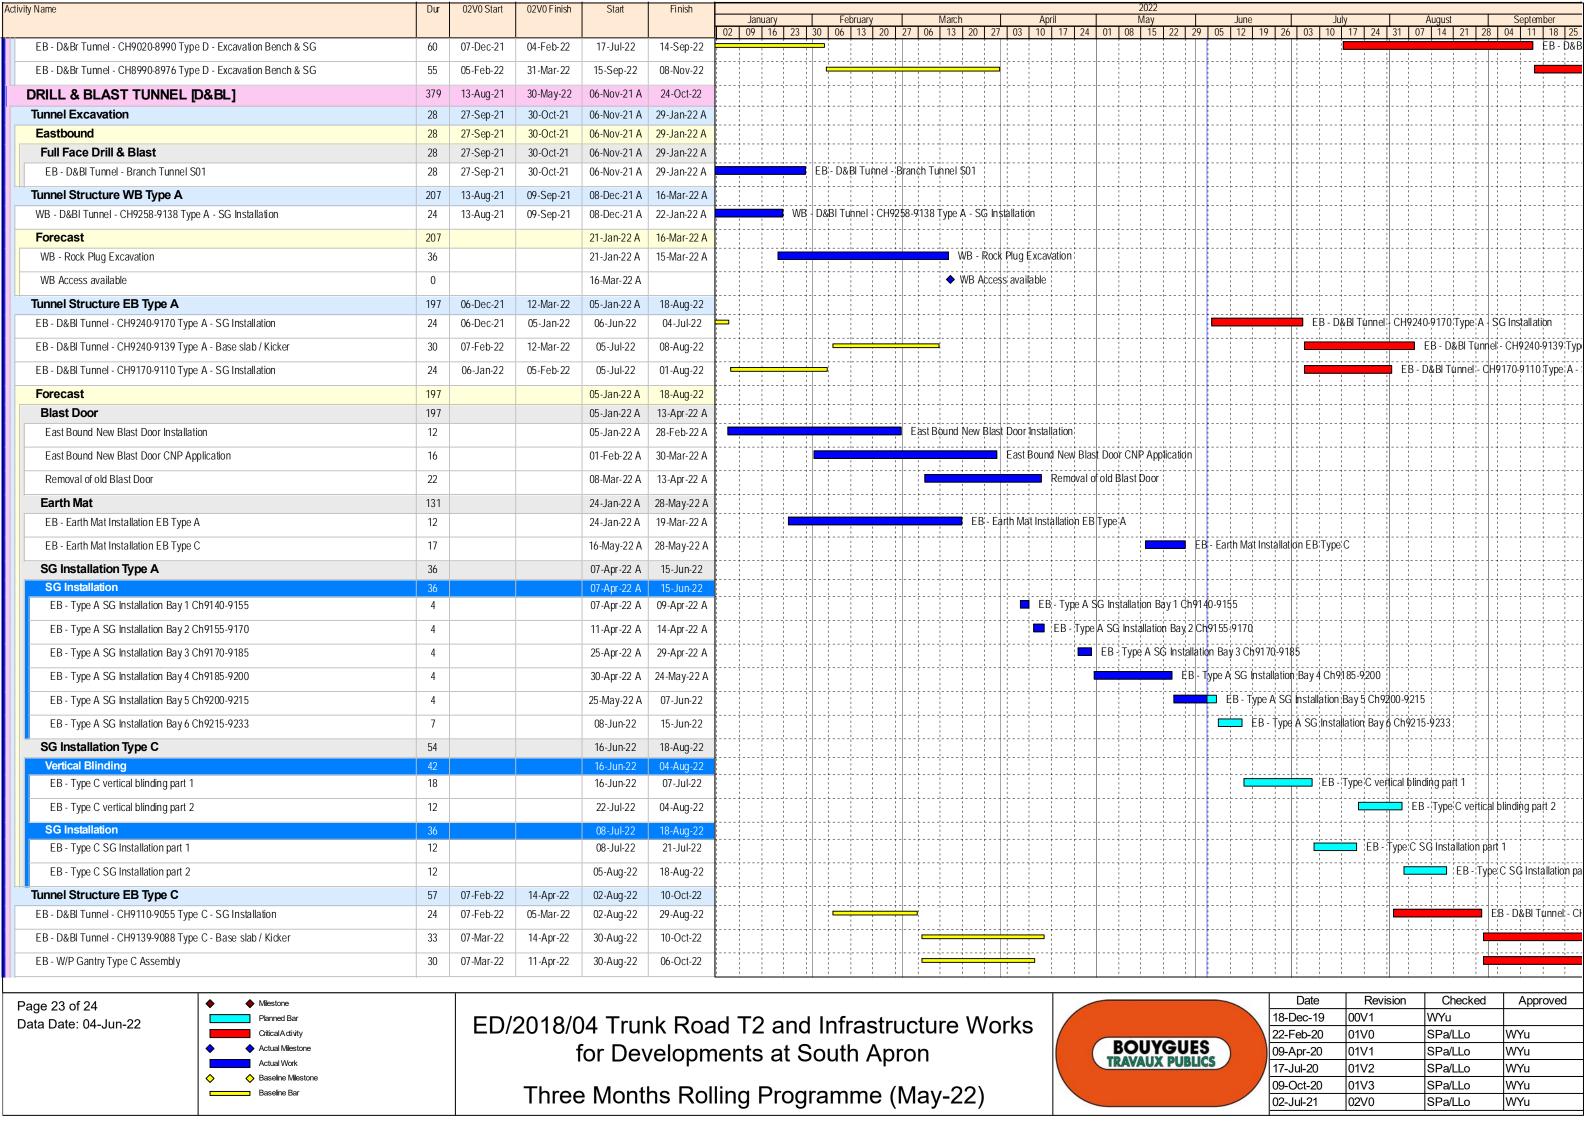

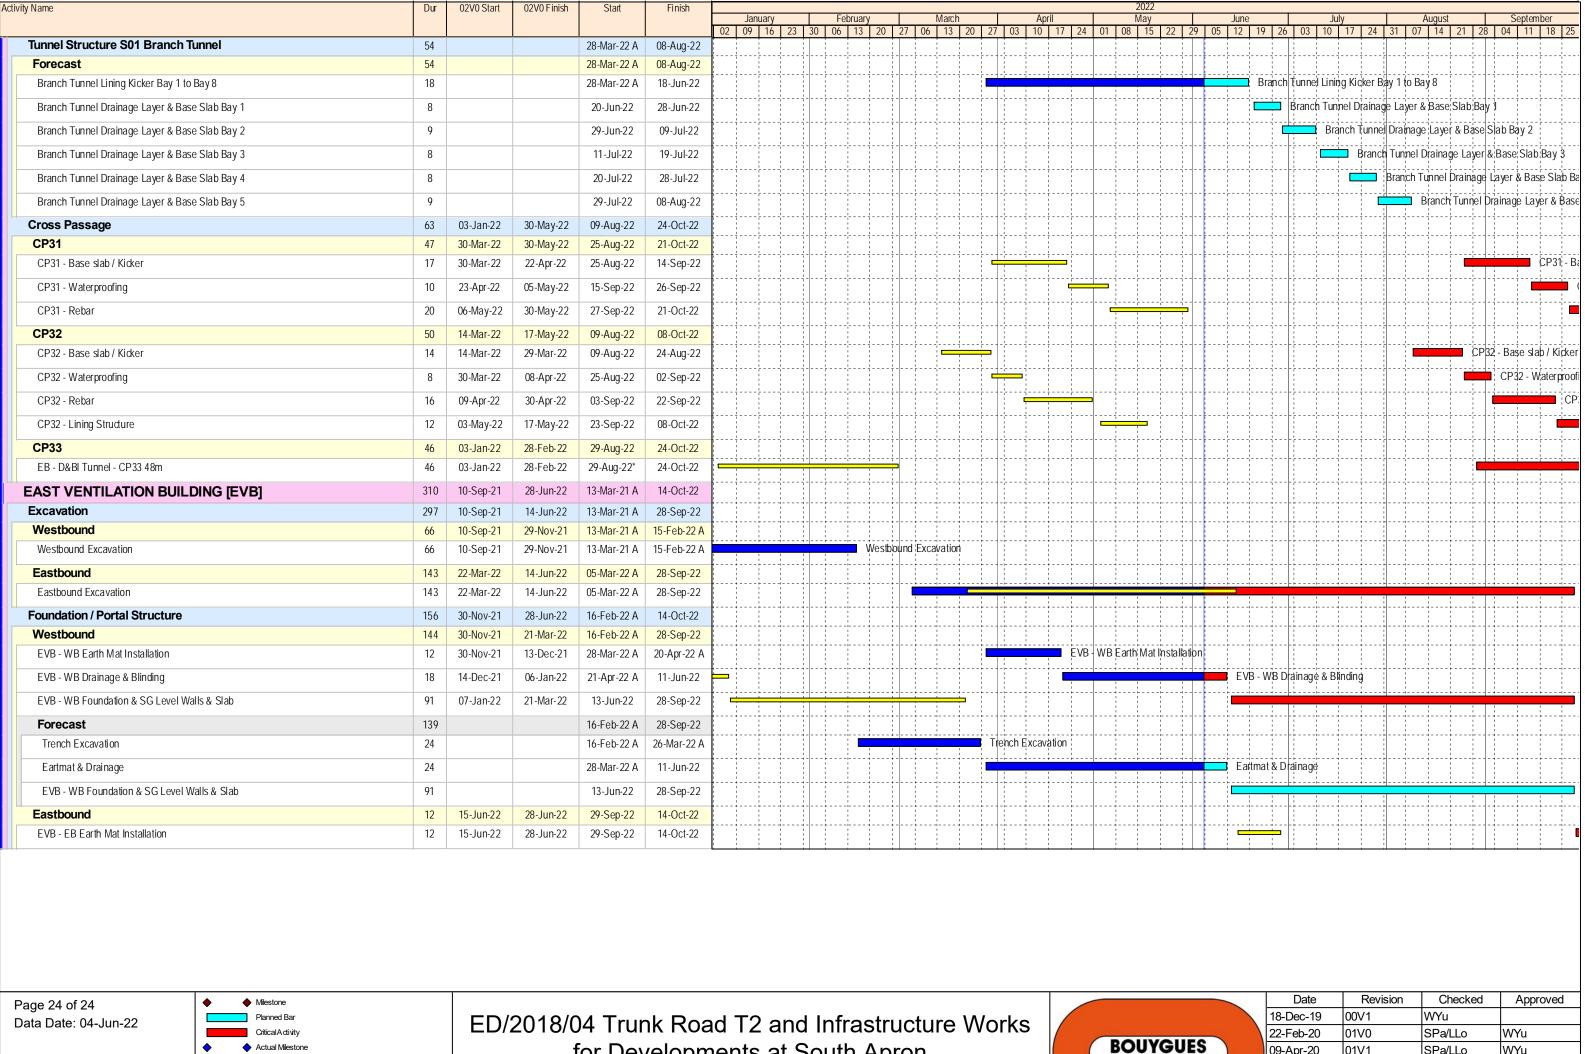

Critical Activity

Actual Milestone
Actual Work

Baseline Bar

Critical Activity

for Developments at South Apron

Three Months Rolling Programme (May-22)

BOUYGUES TRAVAUX PUBLICS 09-Apr-20 01V1 SPa/LLo WYu WYu 17-Jul-20 01V2 SPa/LLo 09-Oct-20 01V3 SPa/LLo WYu 02-Jul-21 02V0 SPa/LLo WYu

APPENDIX O WASTE GENERATED IN THE REPORTING MONTH



Name of Department: CEDD

Monthly Summary Waste Flow Table for 2022 (KT)

Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Contract No. ED/2018/04

	Actu	al Quantities	of Inert C&D	Materials G	Actual Quantities of C&D Wastes Generated Monthly							
Month	a.Total Quantity Generated (a=c+d+e)	b. Hard Rock and Large Broken Broken Contract		d. Reused in Other Projects		f. Imported Fill	g. Metals	h. Paper / Cardboard Packaging	i. Plastics	j. Chemical Waste	k. Others, e.g. general refuse	
	(in '000m ³)	(in '000m ³)	(in '000m ³) (in '000m ³)		(in '000m ³)	(in '000m ³)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)	
January	10.929	2.331	0.000	10.914	0.015	0.000	94.890	0.460	0.000	11.000	0.068	
February	7.698	0.114	0.000	7.601	0.097	0.000	41.250	0.280	0.000	0.000	0.087	
March	17.815	3.844	0.000	17.805	0.010	0.000	17.310	0.000	0.000	0.000	0.086	
April	13.031	0.247	0.000	13.004	0.027	0.000	3.250	0.700	0.000	0.000	0.120	
May	20.807	0.137	0.000	20.798	0.009	0.000	0.000	0.000	0.000	8.000	0.070	
June	36.162	0.047	0.000	0.000	36.162	0.000	0.000	0.260	0.000	4.800	0.069	
Sub-total	106.441	6.720	0.000	70.121	36.320	0.000	156.700	1.700	0.000	23.800	0.500	
July												
August												
September												
October												
November												
December												
Total	106.441	6.720	0.000	70.121	36.320	0.000	156.700	1.700	0.000	23.800	0.500	

Monthly Summary Waste Flow Table

Notes:

- (1) The performance targets are given in ER Appendix 8I Clause 14 and the EM&A Manual(s).
- (2)The waste flow table shall also include C&D materials to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- (4)The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m3. (ER Part 8 Clause 8.8.5 (d) (ii) refers).
