Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# ENVIRONMENTAL MONITORING & AUDIT MONTHLY REPORT

**June 2019** 

Client : Drainage Services Department

Contract Name: Expansion of Sha Tau Kok Sewate Treatment Works -

Environmental Team Services for Baseline Phase – Additional Services for Environmental Team Services at

Early Stage of Construction Phase

Contract No. : CM 8/2018

**EP No.** : EP-517/2017

**Report No.** : 0118/18/ED/0323A

Prepared by: Wingo H. W. So

Reviewed by: Cyrus C. Y. Lai

Certified by: Laborn Leung

Calvin M. P. Leung

Environmental Team Leader Fugro Technical Services Limited



Drainage Services Department

42/F, Revenue Tower

5 Gloucester Road Wan Chai

Hong Kong

Attention: Mr K K Leung

Your reference:

Our reference:

HKDSD206/50/105894

Date:

18 July 2019

BY EMAIL & POST

(email: kkleung04@dsd.gov.hk)

Dear Sirs

Agreement No.: CM 14/2018

Independent Environmental Checker Services for Expansion of Sha Tau Kok Sewage Treatment Works

Environmental Monitoring and Audit Monthly Report (June 2019)

We refer to emails of 8 and 12 July 2019 from Fugro Technical Services Limited attaching the Environmental Monitoring and Audit Monthly Report (June 2019).

We have no further comment and hereby verify the captioned Report in accordance with Clause 3.4 of the Environmental Permit no. EP-517/2017.

Should you have any queries, please do not hesitate to contact the undersigned or our Mr Adi Lee at 2618 2831.

Yours faithfully ANEWR CONSULTING LIMITED

James Choi

Independent Environmental Checker

CPSJ/LYMA/CYYH/lhmh

cc Black & Veatch Hong Kong Limited – Mr Kelvin Chan (email: re.c1.dc1803@gmail.com)
Black & Veatch Hong Kong Limited – Mr Anthony Leung (email: re.em2.dc1803@gmail.com)

Fugro Technical Services Limited – Mr Colin Yung (email: c.yung@fugro.com)

Fugro Technical Services Limited – Mr Calvin Leung (email: c.leung@fugro.com)

Fugro Technical Services Limited – Mr Cyrus Lai (email: c.lai@fugro.com)

**ANewR Consulting Limited** 

Unit 517, 5/F, Tower A, Regent Centre 63 Wo Yi Hop Road, Kwai Chung, Hong Kong Tel: (852) 2618 2831 Fax: (852) 3007 8648

Email: info@anewr.com Web: www.anewr.com



Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel: +852 2450 8233
Fax: +852 2450 6138
Fax: +852 2450 6138
Fe-mail: matlab@fugro.com
Website: www.fugro.com



# **TABLE OF CONTENTS**

<b>EXE</b>	ECUTIVE SUMMARY	1
1.	INTRODUCTION	2
2.	ENVIRONMETNAL MONITORING	4
3.	ENVIRONMENTAL SITE INSPECTION AND AUDIT	9
4.	ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	9
5.	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	9
6.	FUTURE KEY ISSUES	10
7.	CONCLUSIONS	10

# **FIGURES**

Figure 1 Noise Monitoring Stations

Figure 2 Project Boundary

# **LIST OF APPENDICES**

Appendix B Appendix C Appendix D Appendix E Appendix E Appendix E Appendix F Appendix F Appendix G Appendix H Appendix I Appendix I Appendix J Appendix J Appendix M	Appendix A	Construction Programme
Appendix D Appendix E Appendix F Appendix F Appendix G Appendix H Appendix I Appendix I Appendix J Appendix J  Environmental Monitoring Schedules Noise Monitoring Data and Graphical Presentations Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions Site Audit Summary Event and Action Plans Implementation Status of Environmental Mitigation Measures (Construction Phase) Proactive Environmental Protection Proforma	Appendix B	Project Organization Chart
Appendix E Appendix F  Appendix F  Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions  Appendix G  Appendix H  Appendix I  Appendix I  Appendix J  Proactive Environmental Protection Proforma	Appendix C	Calibration Certificates of Monitoring Equipment
Appendix F Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions  Appendix G Appendix H Appendix I Appendix I Appendix J  Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions  Site Audit Summary Event and Action Plans Implementation Status of Environmental Mitigation Measures (Construction Phase) Proactive Environmental Protection Proforma	Appendix D	Environmental Monitoring Schedules
Successful Prosecutions  Appendix G Appendix H Appendix I Appendix J  Successful Prosecutions Site Audit Summary Event and Action Plans Implementation Status of Environmental Mitigation Measures (Construction Phase) Proactive Environmental Protection Proforma	Appendix E	Noise Monitoring Data and Graphical Presentations
Appendix G Appendix H Appendix I Appendix J  Site Audit Summary Event and Action Plans Implementation Status of Environmental Mitigation Measures (Construction Phase) Proactive Environmental Protection Proforma	Appendix F	Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and
Appendix H Appendix I Appendix J  Event and Action Plans Implementation Status of Environmental Mitigation Measures (Construction Phase) Proactive Environmental Protection Proforma		Successful Prosecutions
Appendix I Implementation Status of Environmental Mitigation Measures (Construction Phase) Appendix J Proactive Environmental Protection Proforma	Appendix G	Site Audit Summary
Appendix J Proactive Environmental Protection Proforma	Appendix H	Event and Action Plans
	Appendix I	Implementation Status of Environmental Mitigation Measures (Construction Phase)
Appendix K Waste Flow Table	Appendix J	Proactive Environmental Protection Proforma
	Appendix K	Waste Flow Table

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



### **EXECUTIVE SUMMARY**

i. This is the 1<sup>st</sup> monthly EM&A Report which summaries the impact monitoring results and audit findings for the Project within the period from 27 May 2019 to 30 June 2019.

#### **Exceedances of Action and Limit Levels**

ii. No Action or Limit Level Exceedance was recorded in the reporting period.

# **Complaint, Notifications of Summons and Successful Prosecutions**

iii. No Complaint, Notifications of Summon and Successful Prosecution was recorded in the reporting period.

# **Reporting Change**

iv. There was no reporting change required in the reporting period.

# **Future Key Issues**

# Construction Activities for the Coming Reporting Period

- v. During the coming reporting period, the principal work activities within the site included:
  - Piling Works in Temporary Sewage Treatment Plant (TSTP)
- vi. Potential environmental impacts due to the construction activities, including air quality, noise, water quality, waste, landscape and visual, will be monitored or reviewed. The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirements. The recommended environmental mitigation measures shall be implemented on site and regular inspections as required will be carried out to ensure that the environmental conditions are acceptable.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



# 1. INTRODUCTION

# 1.1 Background

- 1.1.1 The Project in Sha Tau Kok mainly comprises of the following items:
  - i) Increase the treatment capacity of Sha Tau Kok Sewage Treatment Works (STKSTW) to 5,000 m³/day at Average Dry Weather Flow (ADWF) in Phase 1, with suitable allowance to cater for a further increase of treatment capacity to 10,000 m³/day at ADWF in Phase 2;
  - ii) Construct a Temporary Sewage Treatment Plant (TSTP);
  - iii) Demolish the existing Sha Tau Kok Sewage Pumping Station (STKSPS) and decommission the rising main between STKSPS and STKSTW;
  - iv) Construct a new gravity sewer; and
  - v) Decommission the existing submarine outfall and construct a new one.
- 1.1.2 The Project site will be within the existing STKSTW while the construction of the gravity sewers and demolition of STKSPS will be carried out in Sha Tau Kok Town. The proposed submarine outfall will be constructed by Horizontal Directional Drilling (HDD) method under the sea bed of Starling Inlet.
- 1.1.3 Fugro Technical Services Limited (FTS) has been appointed to work as the additional services for Environmental Team services at early stage of construction phase to implement the Environmental Monitoring and Audit (EM&A) programme for the Environmental Permit No. EP-517/2017 Expansion of Sha Tau Kok Sewage Treatment Works.
- 1.1.4 The EM&A programme of this project shall be implemented in accordance with the requirements and procedures set out in the EM&A Manual (AEIAR-207/2017) and the Environmental Permit No. EP-517/2017.
- 1.1.5 A baseline noise monitoring work was conducted between 25 February 2019 and 11 March 2019 and an Environmental Monitoring Report (Noise) Report (Report No.: 0118/18/ED/0259D) had submitted to EPD on 2 April 2019.
- 1.1.6 A baseline water quality monitoring was conducted between 26 February 2019 and 23 Mar 2019 and an Environmental Monitoring Report (Water) Report (Report No.: 0118/18/ED/0307E) had submitted to EPD on 14 Jun 2019.
- 1.1.7 The construction phase and EM&A programme of the Project commenced on 27 May 2019.
- 1.1.8 This is the 1<sup>st</sup> monthly EM&A Report which summaries the impact monitoring results and audit findings for the Project within the period from 27 May 2019 to 30 June 2019.

# 1.2 Project Organization

1.2.1 The Project Organization structure is shown in **Appendix B**. The key personnel contact names and numbers are summarized in **Table 1.1**.

Table 1.1 Contact Information of Kev Personnel

Party	Position	Name	Telephone
Drainage Services Department, HKSAR (DSD)	Engineer	Mr. Gary Leung	2594 7594

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



Party	Position	Name	Telephone
Black & Veatch Hong Kong Limited (B&V)	Resident Engineer	Mr. Anthony Leung	2946 8708
ANewR Consulting Limited (ANEWR)	IEC	Mr. James Choi	2618 2836
Contractor (BK-KS JV)	Environmental Officer	Mr. Justin Cheng	6845 0692
Fugro Technical Services Limited (FTS)	ET Leader	Mr. Calvin Leung	3565 4441

# 1.3 Construction Programme and Activities

- 1.3.1 The construction phase of the Project under the EP commenced on 27 May 2019.
- 1.3.2 The construction programme of the Project is shown in **Appendix A**.

# 1.4 Works undertaken during the month

- 1.4.1 During this reporting period, the principal work activities within the site included:
  - Piling Works in Temporary Sewage Treatment Plant (TSTP)
- 1.4.2 Illustrations of works undertaken during the reporting period are shown in **Table 1.2**:

Table 1.2 Works undertaken Illustrations



Piling Works in Temporary Sewage Treatment Plant (TSTP)

# 1.5 Status of Environmental Licences, Notification and Permits

1.5.1 A summary of the relevant permits, licences and/or notifications on environmental protection for this Contract is presented in **Table 1.3**.

Table 1.3 Environmental Licences, Notification and Permits Summary

Permit / Notification / License	Ref No	Valid From	Valid Till
Environmental Permit	EP-517/2017	15/02/2017	N/A
Wastewater Discharge Licence	WT00033567-2019	02/05/2019	31/05/2024
Registration as a Chemical Waste Producer	5213-652-B2548-01	14/12/2018	N/A
Billing Account	WFG19965	02/01/2019	N/A

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# 2. ENVIRONMETNAL MONITORING

### Noise

# 2.1 Monitoring Methodology & Criteria

- 2.1.1 In accordance with the EM&A Manual, The impact noise monitoring should be carried out at all the designated monitoring stations when there are project-related construction activities undertaken within a radius of 300m from the monitoring stations. Monitoring of Leq(30min) should be carried out at each station at 0700-1900 hours on normal weekdays at a frequency of once a week when construction activities are underway.
- 2.1.2 The monitoring and the QA/QC procedures are as follows:
  - The monitoring station will set at a point 1m from the exterior of the sensitive receivers building façade and set at a position 1.2m above the ground.
  - The battery condition was checked to ensure good functioning of the meter.
  - Parameters such as frequency weighting, the time weighting and the measurement time will set as follows:

frequency weighting : Atime weighting : Fast

measurement time : 30 minutes

- Prior to and after noise measurement, the meter shall be calibrated using the calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement is more than 1.0 dB, the measurement will considered invalid and repeat of noise measurement is required after re-calibration or repair of the equipment.
- The wind speed at the monitoring station shall be checked with the portable wind meter. Noise monitoring should be cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.
- Noise measurement should be paused during periods of high intrusive noise if possible and observation shall be recorded when intrusive noise is not avoided.
- At the end of the monitoring period, the Leq, L10 and L90 shall be recorded. In addition, site conditions and noise sources should be recorded on a standard record sheet.

# Maintenance / Calibration

- The microphone head of the sound level meter and calibrator should be cleaned with a soft cloth at quarterly intervals.
- The sound level meter and calibrator should be calibrated annually by a HOKLAS laboratory or the manufacturer.
- Relevant calibration certificates are provided in Appendix C.

# 2.2 Monitoring Equipment and Detection Limits

2.2.1 As referred to in the Technical Memorandum (TM) issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



Measurements should be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.

- 2.2.2 Noise measurements should not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.
- 2.2.3 The ET is responsible for the provision of the monitoring equipment to ensure that sufficient noise measuring equipment and associated instrumentation are available for carrying out the baseline monitoring, regular impact monitoring and ad hoc monitoring. All the equipment and associated instrumentation shall be clearly labelled.
- 2.2.4 **Table 2.1** summarizes the noise monitoring equipment model used for this project.

Table 2.1 Noise Monitoring Equipment

Manufacturer/ Brand	Model	Equipment	Serial Number
Cacalla	CEL-63X Series	Sound Level Meter	1488269
Casella	CEL-120/1	Sound Calibrator	2383687

# 2.3 Monitoring Parameters and Frequency

2.3.1 **Table 2.2** presents the noise monitoring parameters and frequencies.

Table 2.2 Monitoring Parameters and Frequencies of Noise Monitoring

Parameter	Frequency and Period
LAeq (30min)	At each station at 0700-1900 hours on normal
L10 and L90 will be recorded for reference	weekdays at a frequency of once a week

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com




# 2.4 Monitoring Locations

2.4.1 Noise monitoring was conducted at two designated monitoring stations as described in **Table 2.3** and the monitoring locations are shown in **Figure 1**.

Table 2.3 Location of noise monitoring stations

ID	Noise Sensitive Receivers (NSR)	Description	Type of Measurement*
NM1	NSR 6	Block 45, Sha Tau Kok Chuen	Free-field
NM2	NSR 8	Building along Shun Lung Street	Free-field

Note: \*For Free-field measurement, +3dB(A) should be added to the measured results

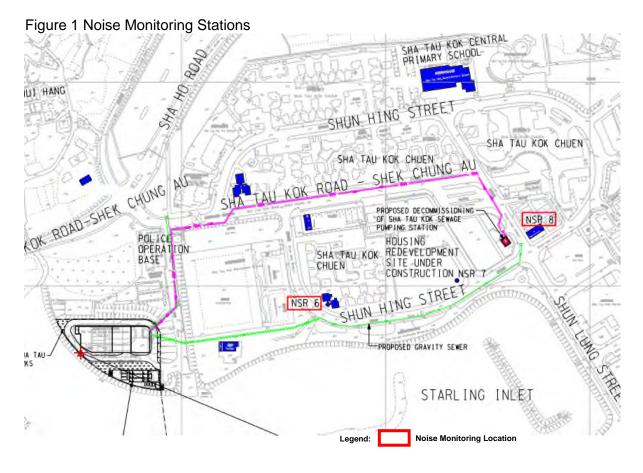

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



### 2.5 Results and Observations

- 2.5.1 The schedule of noise monitoring in reporting period is provided in **Appendix D**.
- 2.5.2 The adopted Action and Limit Levels for noise impact monitoring are presented in **Table 2.4**.

Table 2.4 Action and Limit Levels for Construction Noise

Monitoring Location No.	Description	Action Level	Limit Level
NM1	Block 45, Sha Tau Kok Chuen	When one documented complaint is received from	75 dB(A)*
NM2	Building along Shun Lung Street	any one of the noise sensitive receivers	75 db(A)

Note: \*75 dB(A) for residential premises.

2.5.3 The noise monitoring data are summarized in Table 2.5. Detailed monitoring data are presented in Appendix E.

Table 2.5 Summary of Noise Impact Monitoring Results

Monitoring Station	Construction Noise Level Leq (30min), dB(A)	Baseline Level, dB(A)	Limit Level, dB(A)
NM1	57.7-65.0	65	75
NM2	62.6-70.4	65	75

Note: Leg (30min) was measured at day-time (0700-1900) on normal weekdays.

- 2.5.4 The Event and Action Plan for noise is given in **Appendix H**.
- 2.5.5 No Action or Limit Level Exceedance of noise monitoring was recorded in the reporting period.

# Other factor influencing the monitoring results

2.5.6 There were no other noticeable external factors generally affecting the monitoring results in this reporting period.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# **Water Quality**

- 2.5.7 In accordance with the recommendations of the EIA, water quality EM&A is required during the installation, maintenance and removal of sheetpiles and sediment removal works for construction of diffuser and, during operation of the TSTP and expanded STKSTW.
- 2.5.8 No construction of diffuser and water quality monitoring in the reporting period.

# **Waste Management**

- 2.5.9 Auditing of waste management practices during regular site inspections will confirm that the waste generated during construction are properly, stored, handled and disposed of. The construction Contractor(s) will be responsible for the implementation of any mitigation measures to reduce waste or redress issues arising from the waste materials.
- 2.5.10 The summary of site audited and the implemented environmental mitigation measures in the reporting period are summarized in **Appendix G** and **Appendix I**.
- 2.5.11 Monthly summary of waste flow table is detailed in Appendix K

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# 3. ENVIRONMENTAL SITE INSPECTION AND AUDIT

# 3.1 Site Inspection

- 3.1.1 Regular site inspections will be carried out by the ET once per week during construction phase.
- 3.1.2 In the reporting period, site inspections were carried out on 29 May 2019, 5, 12, 19 and 26 June 2019.
- 3.1.3 The summary of the site audits are given in **Appendix G**.

# 4. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

- 4.1 Complaints, Notification of Summons and Successful Prosecution
- 4.1.1 No complaints, notification of summons or successful prosecutions were received in the reporting period.
- 4.1.2 Cumulative complaint log, summaries of complaints, notification of summons and successful prosecutions are presented in **Appendix F.**

# 5. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

# 5.1 Implementation Status

5.1.1 The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Reports, the EP and the EM&A Manuals. The implementation status of the mitigation measures during the reporting period is summarized in **Appendix I**.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



# 6. FUTURE KEY ISSUES

# 6.1 Construction Works for the Coming Month

- 6.1.1 During the coming reporting period, the principal work activities within the site included:
  - Piling Works in Temporary Sewage Treatment Plant (TSTP)

# 6.2 Key Issues for the Coming Month

- 6.2.1 Potential environmental impacts due to the construction activities, including air quality, noise, water quality, waste, landscape and visual, will be monitored or reviewed. The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirement. The recommended environmental mitigation measures shall be implemented on site and regular inspections as required will be carried out to ensure that the environmental conditions are acceptable.
- 6.2.2 The anticipated impact of principal work activities within the site and the recommended mitigation measures are shown in **Appendix J**.

# 6.3 Monitoring Schedules for the Coming Months

6.3.1 The tentative schedules for environmental monitoring in the coming months are provided in **Appendix D**.

# 7. CONCLUSIONS

- 7.1.1 No Action or Limit Level Exceedance was recorded in the reporting period.
- 7.1.2 No complaints, notification of summons or successful prosecutions were received in the reporting period.
- 7.1.3 There was no reporting change required in the reporting period.
- 7.1.4 Potential environmental impacts due to the construction activities, including air quality, noise, water quality, waste, landscape and visual, will be monitored or reviewed. The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirements. The recommended environmental mitigation measures shall be implemented on site and regular inspections as required will be carried out to ensure that the environmental conditions are acceptable.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# Figure 2

**Project Boundary** 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com







Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# Appendix A

**Construction Programme** 

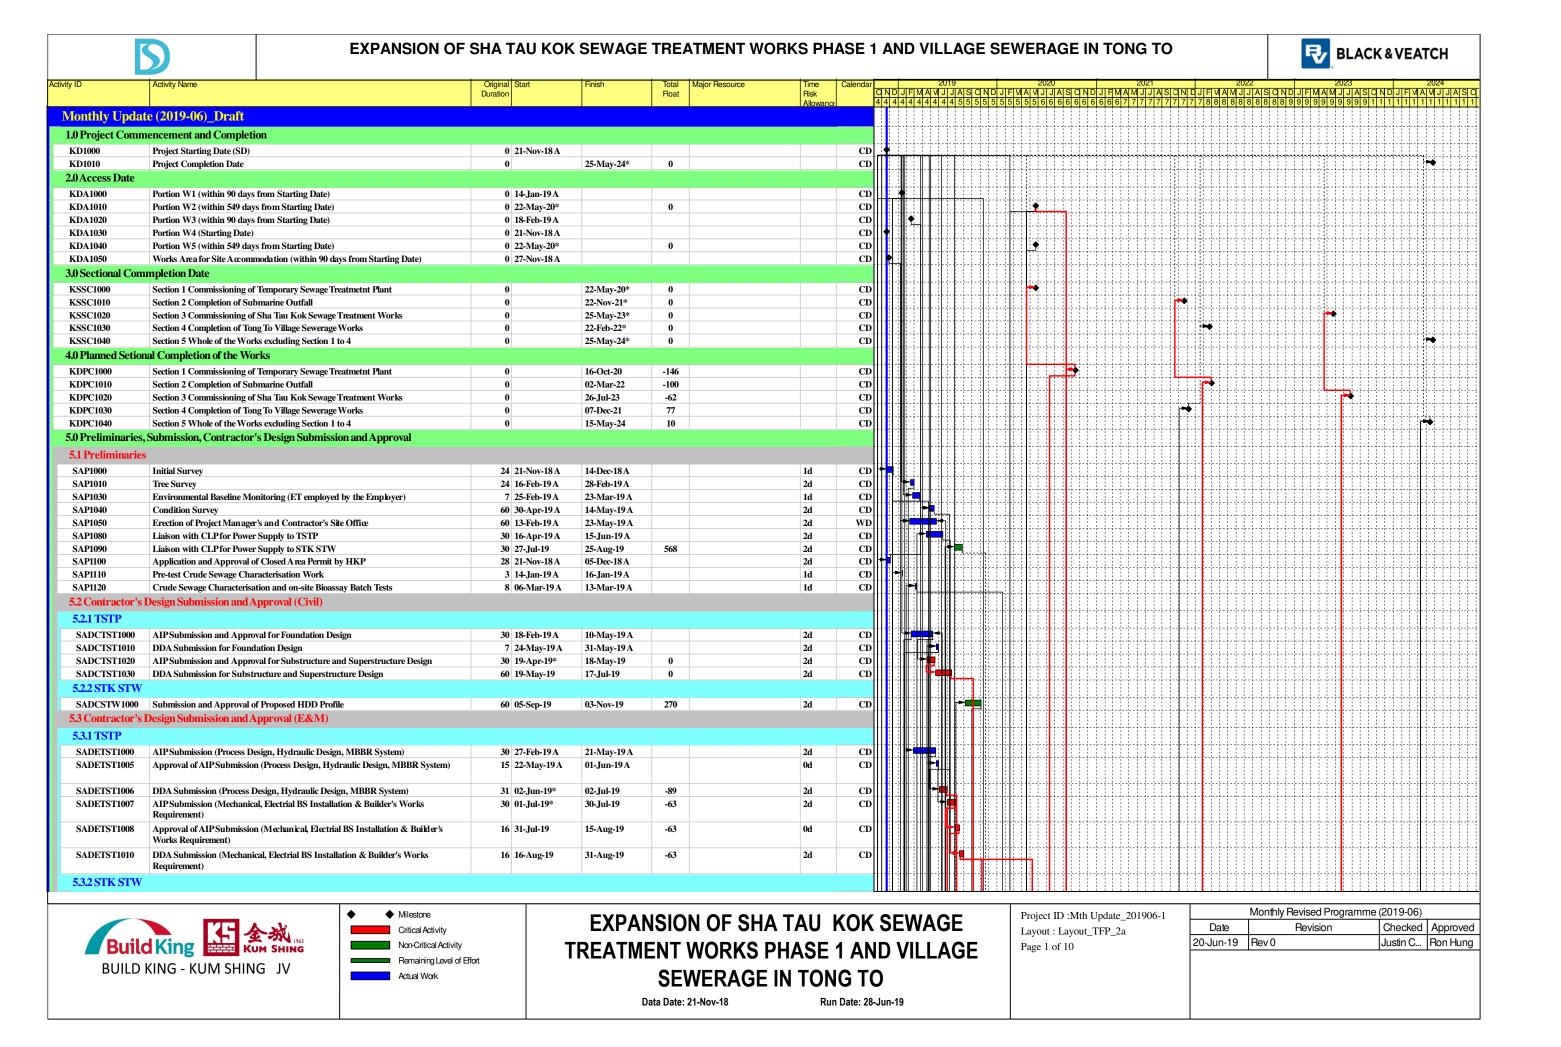

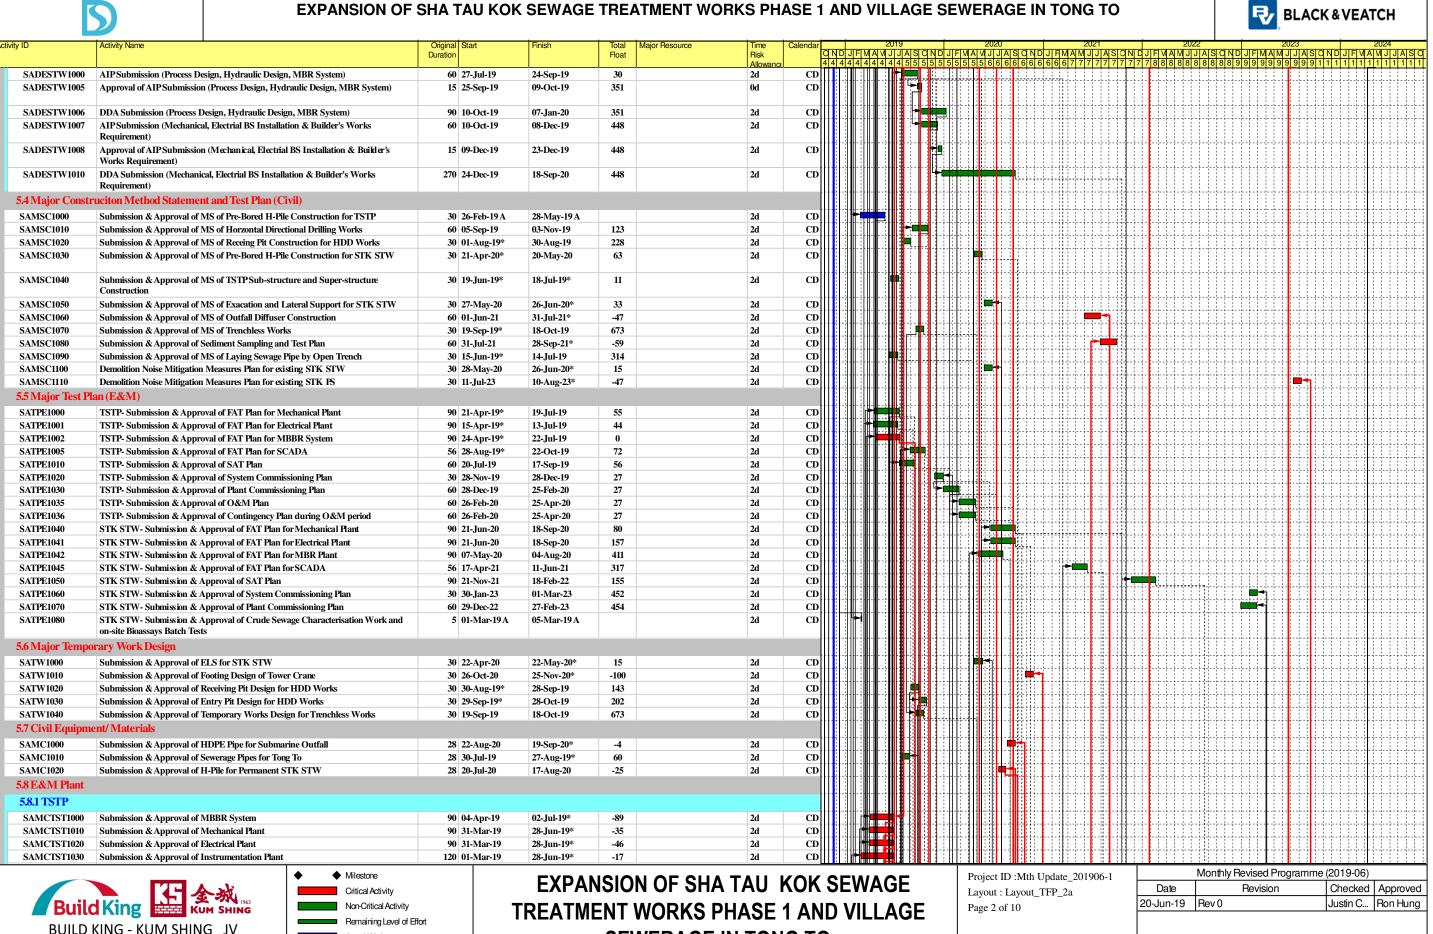






# **SEWERAGE IN TONG TO**

Monthly Revised Programme (2019-06)			
Date	Revision	Checked	Approved
20-Jun-19	Rev 0	Justin C	Ron Hung

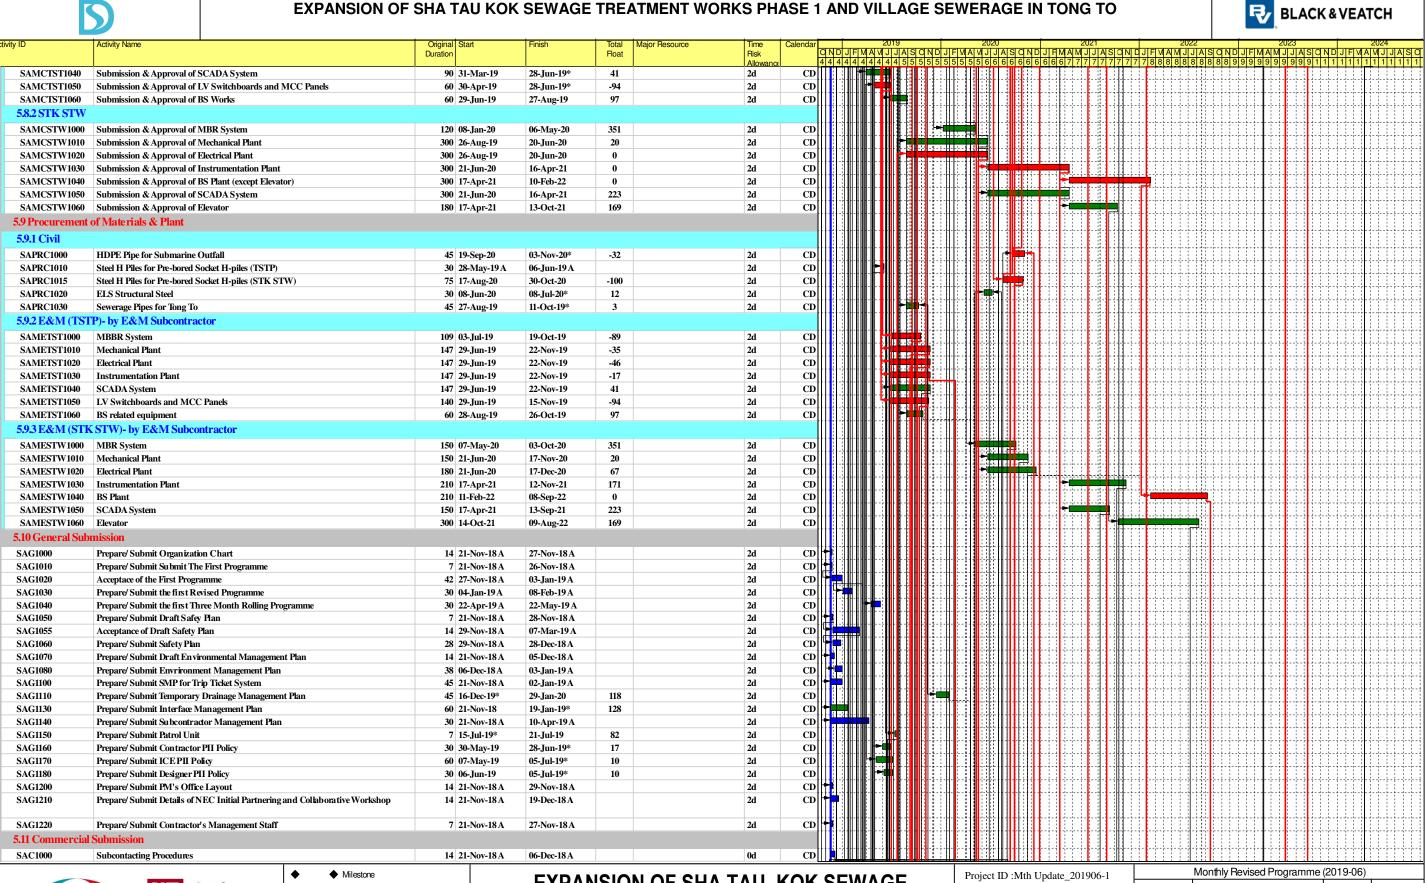






Project ID :Mth Update_20190
Layout : Layout_TFP_2a

Layout	. Layo
Page 3	of 10

Monthly Revised Programme (2019-06)			
Date	e Revision Checked Approve		
20-Jun-19 Rev 0		Justin C	Ron Hung

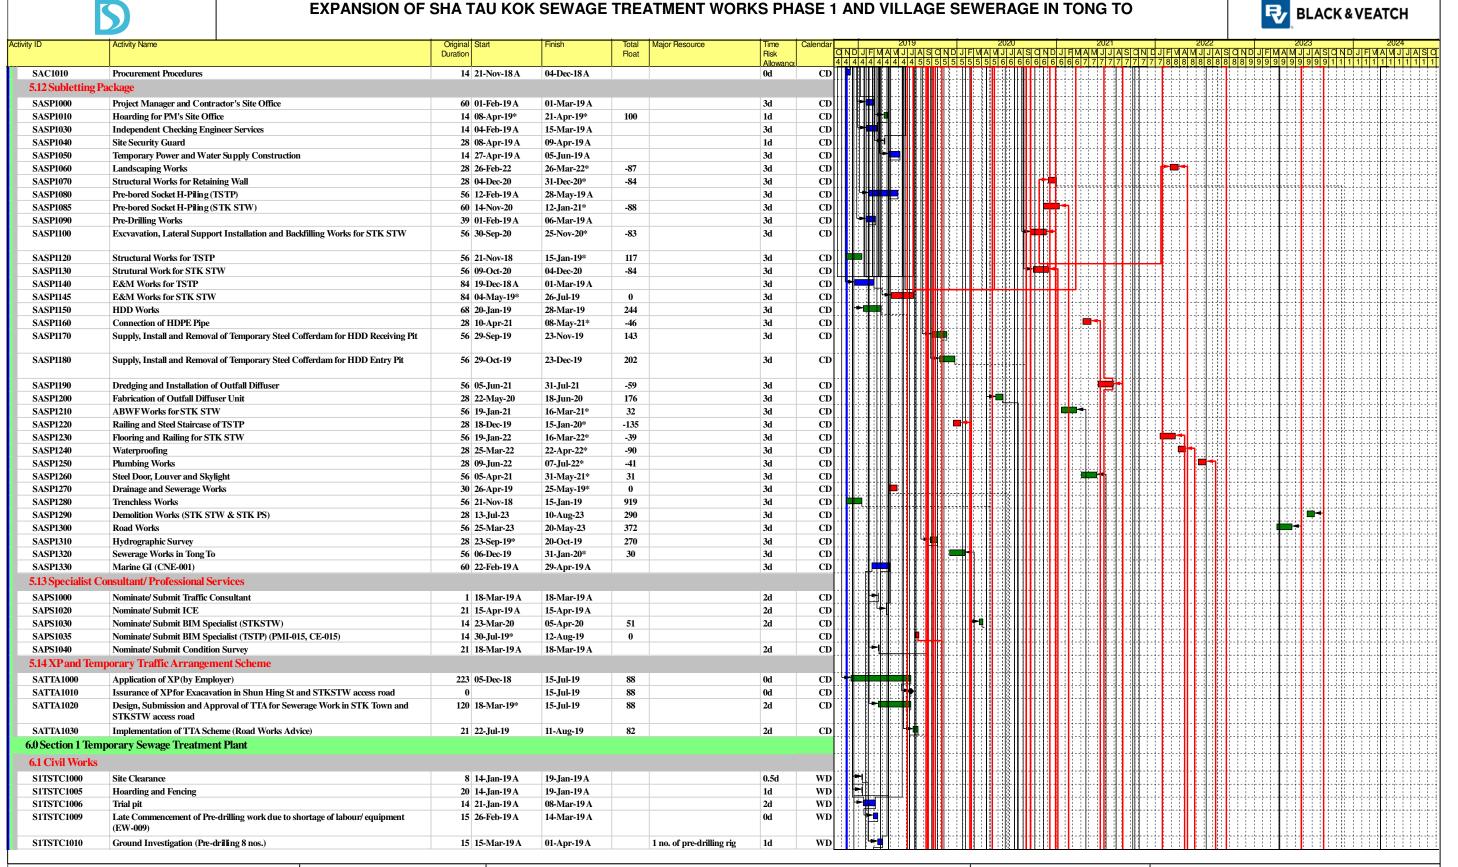






Project ID :Mth Update_201906-1
Layout : Layout_TFP_2a

24,50			,
Page	4 0	of 10	)

Monthly Revised Programme (2019-06)				
Date	Date Revision Checked Approved			
20-Jun-19 Rev 0		Justin C	Ron Hung	

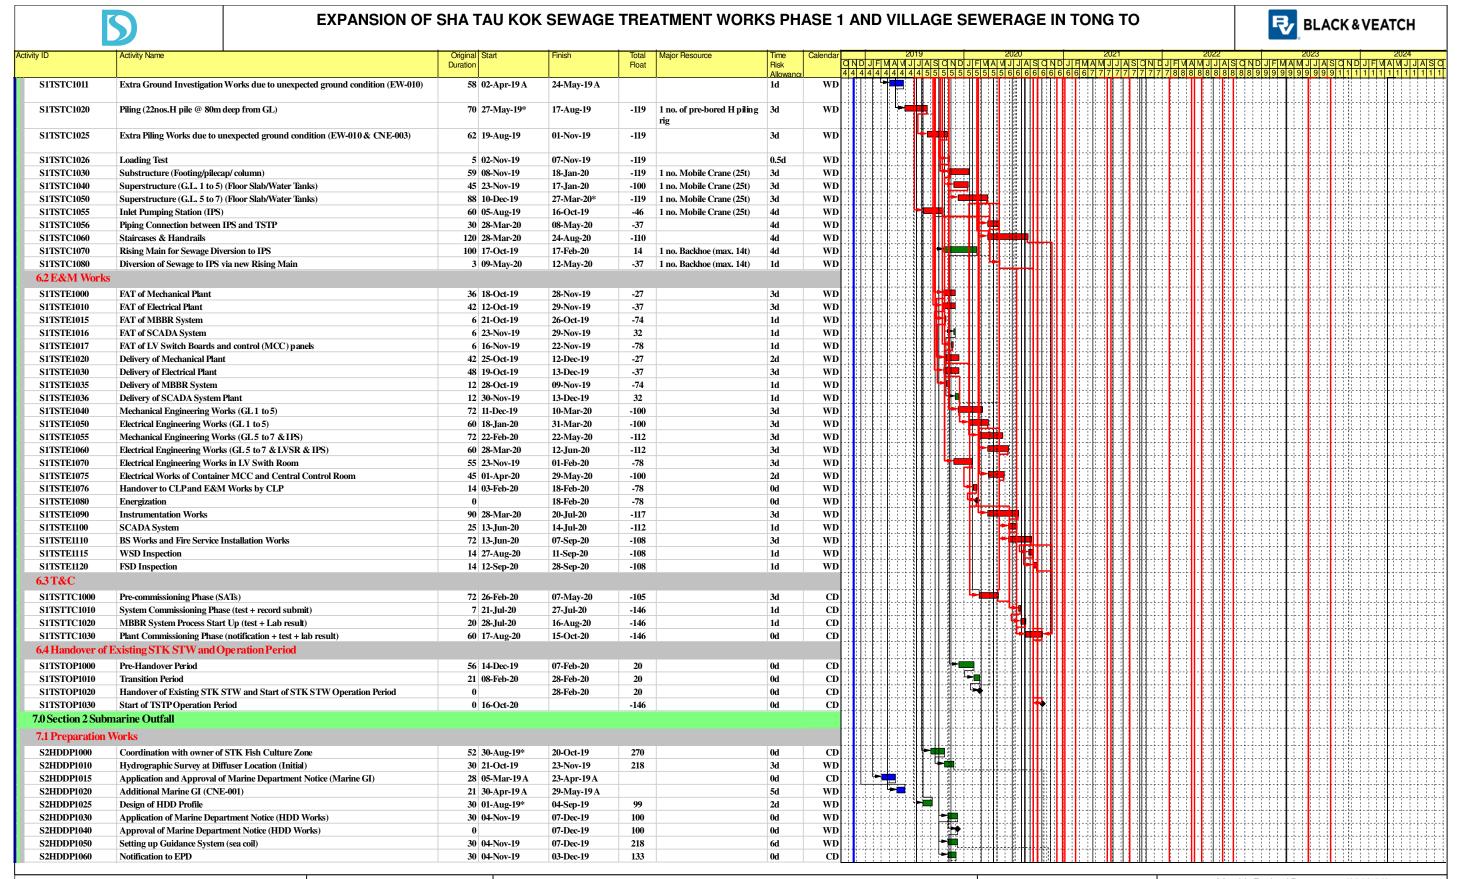






Data Date: 21-Nov-18 Run Date: 28-Jun-19

Project ID :Mth Update\_201906-1 Layout : Layout\_TFP\_2a

•			•
Page	5	of	10

Monthly Revised Programme (2019-06)				
Date	Revision Checked Approved			
20-Jun-19 Rev 0		Justin C	Ron Hung	

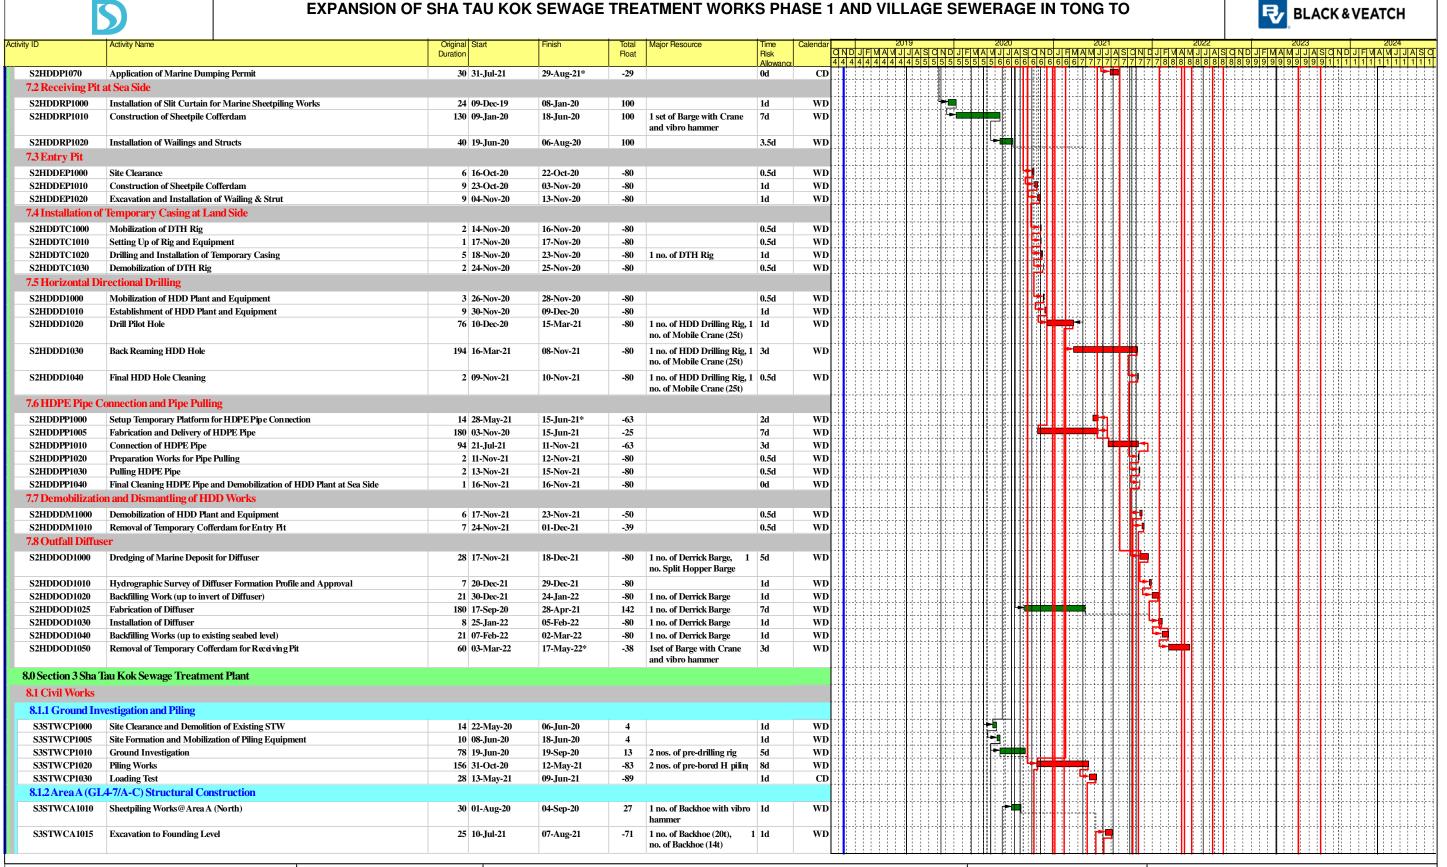





Project ID :Mth Update_201906-1
Layout : Layout_TFP_2a

•				
Page	6	$\alpha$ f	1	

Monthly Revised Programme (2019-06)				
Date	Revision Checked Approved			
20-Jun-19 Rev 0		Justin C	Ron Hung	

#### EXPANSION OF SHA TAU KOK SEWAGE TREATMENT WORKS PHASE 1 AND VILLAGE SEWERAGE IN TONG TO BLACK & VEATCH Float Allowan 54 09-Aug-21 WD S3STWCA1040 12-Oct-21 -71 3d -71 3d WD S3STWCA1050 1st Basement Floor- Wall Sem 54 13-Oct-21 15-Dec-21 S3STWCA1070 Ground Floor- Base Slab & Wall Stem 78 16-Dec-21 23-Mar-22 -71 3d WD S3STWCA1080 1st Floor- Base Slab & Wall Stem 14-Jul-22 -71 3d WD 90 24-Mar-22 S3STWCA1090 Roof Floor- Base Slab and Upstand Wall 45 15-Jul-22 05-Sep-22 -71 2d WD 8.1.3 Area B (GL1-4/A-C) Structural Construction S3STWCB1005 Sheetpiling Works@Area B (West) 14 08-Jul-20 23-Jul-20 1 no. of Backhoe with vibro 1d WD S3STWCB1006 Excavation to Founding Level 24 10-Jun-21 09-Jul-21 -71 1 no. of Backhoe (20t). WD no, of Backhoe (14t) S3STWCB1010 30 10-Jul-21 -51 WD 1st Basement Floor- Base Slab 13-Aug-21 WD S3STWCB1015 Installation of Raking Struts 24 14-Aug-21 -51 1d 10-Sep-21 S3STWCB1020 1st Basement Floor- Remaining Base Slab & Wall Stem 54 11-Sep-21 16-Nov-21 -51 3d WD Backfill and Remove ELS -51 1 1d WD S3STWCB1030 18 17-Nov-21 07-Dec-21 1 no. of Backhoe (20t). no, of Backhoe (14t) S3STWCB1040 Ground Floor- Base Slab & Wall Stem 72 08-Dec-21 08-Mar-22 -51 WD S3STWCB1050 1st Floor- Base Slab & Wall Stem 60 09-Mar-22 23-May-22 -51 3d WD S3STWCB1060 Roof Floor- Base Slab and Upstand Wall 42 24-May-22 13-Jul-22 49 2d WD 8.1.4 Area C (GL 1-4//C-G) Structural Construction S3STWCC1005 Sheetpiling Works@Area C(West) 14 19-Jun-20 07-Jul-20 4 1 no. of Backhoe with vibro 1d WD WD 07-Jul-20 S3STWCC1006 4 Handover to HDD Subcontractor S3STWCC1007 HDD Subcontractor Handover to Contractor after HDD Works 23-Nov-21 -50 WD S3STWCC1008 -50 1 no. of Backhoe (20t). 1 1d WD Excavation to Founding Level 18 24-Nov-21 14-Dec-21 no, of Backhoe (14t) S3STWCC1010 21 15-Dec-21 11-Jan-22 -50 1d WD 1st Basement Floor- Base Slab S3STWCC1015 Installation of Raking Struts 18 12-Jan-22 04-Feb-22 -50 1d WD S3STWCC1020 1st Basement Floor- Remaining Base Slab & Wall Stem 42 05-Feb-22 25-Mar-22 -50 WD 2d S3STWCC1030 Backfill and Remove ELS 18 26-Mar-22 19-Apr-22 -50 1 no. of Backhoe (20t), 1 1d WD no. of Backhoe (14t) S3STWCC1040 Ground Floor- Base Slab & Wall Stem 54 20-Apr-22 24-Jun-22 -50 3d WI S3STWCC1050 1st Floor- Base Slab & Wall Stem 54 25-Jun-22 27-Aug-22 -35 3d WD S3STWCC1060 Roof Floor- Base Slab and Upstand Wall 45 29-Aug-22 22-Oct-22 -35 2d WD 8.1.5 Area D (GL 4-7/ C-G) Structural Construction WD S3STWCD1010 Excavation to Founding Level of Aerobic Tank no. 4 & 5 8 25-Nov-20 03-Dec-20 -83 1 no. of Backhoe (20t), 1 1d no. of Backhoe (14t) S3STWCD1020 Aerboic Tanks no. 4 & 5- Base Slab 14 04-Dec-20 19-Dec-20 -79 1d WD S3STWCD1030 Aerboic Tanks no. 5- Wall Stem 21 21-Dec-20 16-Jan-21 -79 1d WD WD S3STWCD1040 Aerhoic Tanks no 4. Wall Stem 14 18-Jan-21 02-Feb-21 -79 14 Handover Aerboic Tank no. 5 to HDD Subcontactor for Temp Water Tank WD S3STWCD1050 16-Jan-21 -34 WD S3STWCD1060 Handover Aerboic Tanks no. 4 to Tower Crane Subcontractor 02-Feb-21 -79 0dS3STWCD1070 14 03-Feb-21 22-Feb-21\* -79 1d WD Erection of Tower Crane (TC-01) HDD Subcontractor Handover to Contractor after HDD Works 23-Nov-21 -42 0d WD S3STWCD1080 Dismantling of Tower Crane 5 24-Nov-21 29-Nov-21 -42 WD S3STWCD1090 0.5d -42 WD S3STWCD1100 Excavation to Founding Level (Remaining Structure in 1st Basement Floor) 12 30-Nov-21 13-Dec-21 1 no. of Backhoe (20t). 1 1d no, of Backhoe (14t) S3STWCD1110 1st Basement Floor- Base Slab 18 14-Dec-21 06-Jan-22 -42 1d WD 28-Feb-22 S3STWCD1120 1st Basement Floor- Wall Stem 42 07- Jan-22 -42 2d WD S3STWCD1140 Ground Floor- Base Slab & Wall Stem 54 01-Mar-22 06-May-22 -42 3d WD S3STWCD1150 1st Floor- Base Slab & Wall Stem WD 54 07-May-22 12-Jul-22 -42 3d S3STWCD1160 Roof- Base Slab and Upstand Wall 30 13-Jul-22 -42 1d WD 16-Aug-22 8.1.6 Area E (GL 4-8/FS Tanks) Structural Construction S3STWCE1000 Sheetpiling Works@Area E (South) 21 08-Jul-20 31-Jul-20 27 1 no. of Backhoe with vibro 1d WD



S3STWCE1030 Backfill and Remove ELS

Excavation to Founding Level

1st Basement Floor- Base Slab

**Installation of Raking Struts** 

1st Basement Floor- Remaining Base Slab, Wall Stem & Ceilng

S3STWCE1005

S3STWCE1010

S3STWCE1020



24 17-Aug-22

30 15-Sep-22

30 22-Oct-22

72 26-Nov-22

21 25-Feb-23

# EXPANSION OF SHA TAU KOK SEWAGE TREATMENT WORKS PHASE 1 AND VILLAGE SEWERAGE IN TONG TO

WD

WD

WD

WD

1d

3d

-42

-42

-42

-42

348

1 no. of Backhoe (20t),

14-Sep-22

21-Oct-22

25-Nov-22


24-Feb-23

21-Mar-23

Project ID :Mth Update_201906-1
Layout : Layout_TFP_2a

Layout	. т	ayc
Page 7	of	10

	Monthly Revised Programme (2019-06)								
Date	Revision	Checked	Approved						
20-Jun-19	Rev 0	Justin C	Ron Hung						

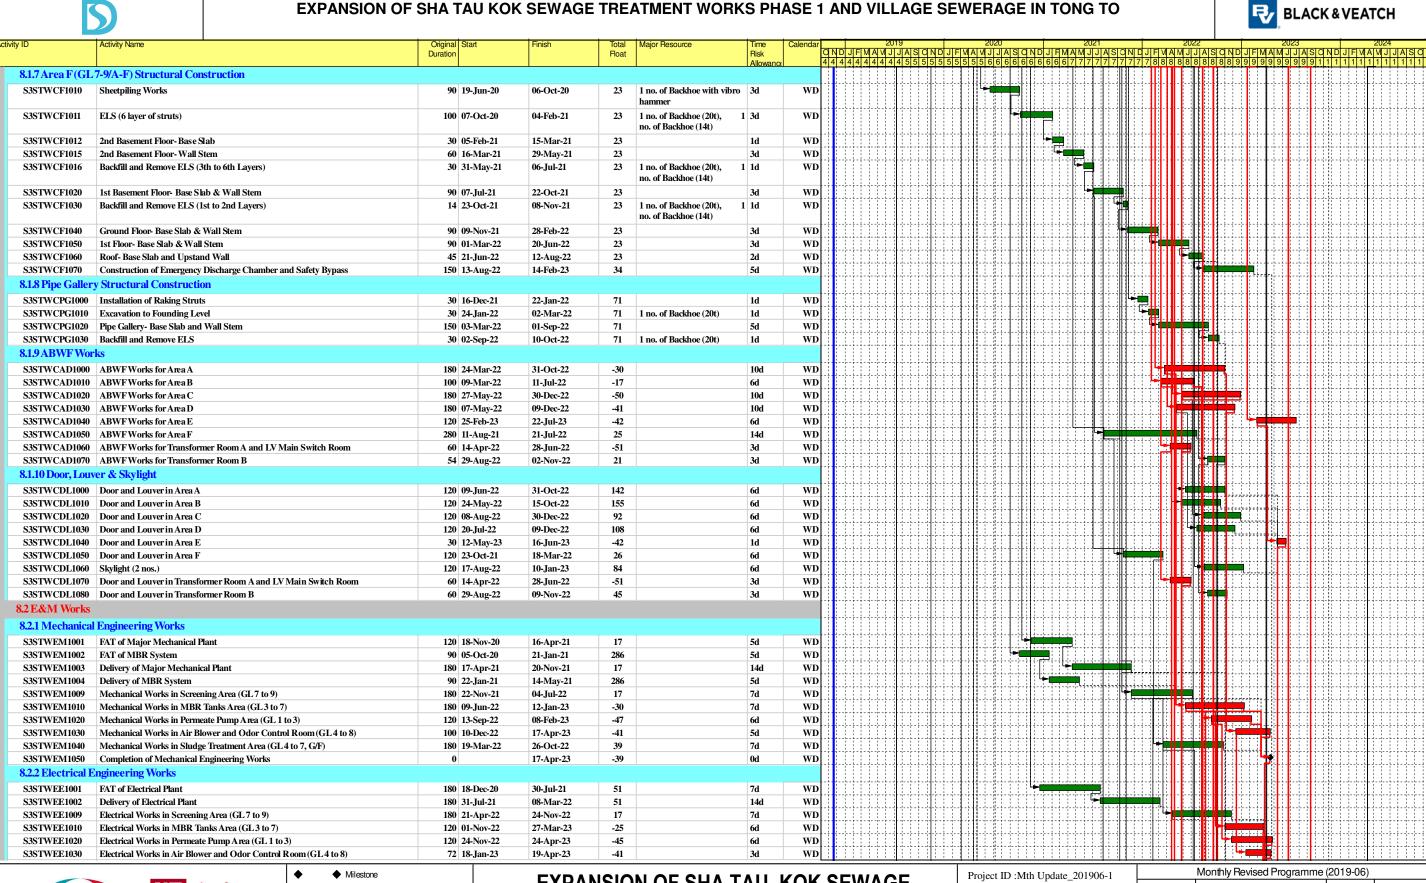





Project II	:Mth Update_201906
Layout : I	_ayout_TFP_2a
Page 8 of	10

01900-1							
	Date	Revision	Checked	Approved			
	20-Jun-19	Rev 0	Justin C	Ron Hung			

#### EXPANSION OF SHA TAU KOK SEWAGE TREATMENT WORKS PHASE 1 AND VILLAGE SEWERAGE IN TONG TO BLACK & VEATCH Float Allowar Electrical Works in Sludge Treatment Area (GL 4 to 7, G/F) 120 15-Aug-22 07-Jan-23 6d WD WD S3STWEE1050 Electrical Works in Transformer Room A 30 29-Jun-22 -51 1d 03-Aug-22 S3STWEE1051 Electrical Works in Transformer Room B 30 03-Nov-22 21 1d WD Electrical Works in LV Main Switch Room WD S3STWEE1060 30 29-Jun-22 03-Aug-22 -51 1d S3STWEE1061 CLP Handover Inspection for Transformer Room A 21 04-Aug-22 27-Aug-22 -51 1d WD WD S3STWEE1062 Handover of Transformer Room A to CLP -51 27-Aug-22 0dS3STWEE1063 Transformer A Installation and E&M Works by CLP 21 29-Aug-22 22-Sep-22 -51 bθ WD WD S3STWEE1064 Energization of Transformer Room A 22-Sep-22 -51 0dS3STWEE1065 CLP Handover Inspection for Transformer Room B 21 08-Dec-22 04-Jan-23 21 1d WD S3STWEE1066 Handover of Transformer Room B to CLP 04-Jan-23 21 0d WD WD S3STWEE1067 Transformer B Installation and E&M Works by CLP 21 05-Jan-23 01-Feb-23 21 0dS3STWEE1068 Energization of Transformer Room B 01-Feb-23 21 0d WD Electrical Works in MCC Room and Central Control Room -50 6d WD S3STWFE1070 120 13-Sep-22 08-Feb-23 Completion of Electical Engineering Works -45 0d WD S3STWEE1080 24-Apr-23 8.2.3 Instrumentation Works S3STWEI1000 Delivery of Instrumentation Plant 90 13-Nov-21 04-Mar-22 136 7d WD S3STWEI1005 Instrumentation Works in Screening Area (GL 7 to 9) 90 14-Mar-22 04-Jul-22 129 3d WD Instrumentation Works in MBR Tanks Area (GL 3 to 7) WD S3STWEI1010 90 24-Sep-22 12-Jan-23 -30 3d -47 WD S3STWF11020 Instrumentation Works in Post MBR Treatment Area (GL 1 to 3) 72 07-Nov-22 04-Feb-23 3d S3STWEI1030 Completion of Instrumentation Works 04-Feb-23 -47 0d WD 8.2.4 SCADA System S3STWES1000 FAT of SCADA System 120 14-Sep-21 10-Feb-22 179 6d WD 66 11-Feb-22 03-May-22 179 WD S3STWFS1010 Delivery of SCADA System 3d S3STWES1020 Installation and Setup of SCADA System 65 09-Feb-23 29-Apr-23 -50 3d WD **8.2.5 BS Works** S3STWEBS1000 BS Works in STK STW 180 24-Oct-22 03-Jun-23 -35 WD S3STWEBS1005 WSD Inspection 24 11-May-23 08-Jun-23 -35 WD 24 17-Jun-23 15-Jul-23 -42 1d WD S3STWEBS1010 WD S3STWEBS1020 Acceptance of FSD 15-Jul-23 -42 S3STWEBS1030 Delivery and Installation of Elevator 60 10-Aug-22 21-Oct-22 136 3d WD S3STWEBS1040 Inspection of Elevator 136 2d WD 14 22-Oct-22 07-Nov-22 8.2.6 Testing and Commissioning S3STWTC1000 Pre-Commissioning Phase (SAT) 180 23-Sep-22 21-Mar-23 -61 7d CD S3STWTC1010 System Commissioning Phase -62 7 30-Apr-23 06-May-23 MBR System Process Start Up 21 07-May-23 -62 S3STWTC1020 27-May-23 14d CD S3STWTC1025 O&M Training and Attachment Training 21 22-Mar-23 19-Apr-23 -17 0.5d WD Plant Commissioning S3STWTC1030 60 28-May-23 26-Jul-23 -62 14d CD 9.0 Section 4 Tong To Village Sewerage Works 22-May-20 S4TTS1005 Fabrication and Delivery of PE Pine 180 11-Oct-19 7d WD 2 S4TTS1006 Branch 1 Sewerage Pipe 60 24-Dec-20 10-Mar-21 Backhoe (max. 7t) WD S4TTS1010 Branch 2 Sewerage Pipe 30 11-Mar-21 17-Apr-21 60 WD Backhoe (max. 7t) 1d Branch 3 Sewerage Pipe S4TTS1020 180 22-May-20 23-Dec-20 Backhoe (max. 7t) 7d WD WD S4TTS1030 Branch 4 Sewerage Pipe 21 19-Apr-21 13-May-21 Backhoe (max. 7t) 1d Branch 5 Sewerage Pipe S4TTS1040 60 14-May-21 26-Jul-21 Backhoe (max. 7t) 3d WD S4TTS1050 21 27-Jul-21 60 Backhoe (max. 7t) 1d WD Branch 6 Sewerage Pipe 19-Aug-21 S4TTS1060 Branch 7 Sewerage Pipe 60 20-Aug-21 01-Nov-21 60 Backhoe (max. 7t) 3d WD S4TTS1070 Branch 8 Sewerage Pipe 31 02-Nov-21 60 1d WD 07-Dec-21 Backhoe (max. 7t) 10.0 Whole of the Works excluding the Works in Section 1 to 4 10.1 Sewerage Works in STK Town 10.1.1 Stream 1 S5OWS1000 Open Trench DN355 PE (STKSTW1002 to STKSTW1007, 225m) 240 12-Aug-19 WD 03-Jun-20 411 1 no. of Backhoe (max. 20t) 14d WD S50WS1010 Trenchless DN355 PE (STKSTW1007 to STKSTW1009, 130m) 16-Feb-21 411 210 04-Jun-20 1set of Trenchless Plant and 10d eauipment



Trenchless DN500 PE (STKSTW1009 to Emergency Discharge Chamber)

S5OWS1020

10.1.2 Stream 2



120 17-Feb-21

14-Jul-21

411

# EXPANSION OF SHA TAU KOK SEWAGE TREATMENT WORKS PHASE 1 AND VILLAGE SEWERAGE IN TONG TO

1set of Trenchless Plant and 6d

WD

Project ID :Mth Update_20190
Layout : Layout_TFP_2a
Page 9 of 10

Monthly Revised Programme (2019-06)							
Date	Revision	Checked	Approved				
20-Jun-19	Rev 0	Justin C	Ron Hung				

#### EXPANSION OF SHA TAU KOK SEWAGE TREATMENT WORKS PHASE 1 AND VILLAGE SEWERAGE IN TONG TO BLACK & VEATCH Float S50WS1030 Open Trench DN500 PE (STKSTW1102 to STKSTW1009, 32m) 45 15-Jul-21 1 no. of Backhoe (max. 14t) 3d WD 04-Sep-21 WD S5OWS1040 Open Trench DN500 PE (Existing STK3022 to STKSTW1102, 80m) 411 1 no. of Backhoe (max. 14t) 6d 120 06-Sep-21 29-Jan-22 Retaining Wall RW1 (4 bays) 140 19-Aug-23 05-Feb-24 1 no. of Backhoe (max. 14t) 6d WD 10.3 Road & Drainage Works in STK STW S5OWRD1000 Drainage Works in EVA 120 19-Aug-23 12-Jan-24 50 1 no. of Backhoe (max. 14t) 6d WD Road Works of EVA WD S5OWRD1010 72 22-Dec-23 21-Mar-24 1 no. of Backhoe (max. 14t) 3d 10.4 Demolition of STK PS S5OWDPS1000 Decommissioning of STK PS 7 10-Aug-23 17-Aug-23 -40 0.5d WD 176 WD S5OWDPS1010 Demolition of STK PS 30 18-Aug-23 21-Sep-23 1d 10.5 Decommissioning of Existing Rising Main in STK Town S5OWDRM1000 Grouting of Existing Rising Main 21 22-Sep-23 18-Oct-23 176 0.5d WD 10.6 Decommissioning of TSTP & Existing Submarine Outfall S5OWDSO1000 Dismantling of TSTP 30 27-Jul-23 30-Aug-23 156 1d WD S5OWDSO1010 Grouting of Existing Submarine Outfall 7 31-Aug-23 07-Sep-23 209 0.5d WD 10.7 Architectural Works of STK STW S5OWA 1000 Waterproofing 100 15-Sep-22 14-Jan-23 -71 5d WD S5OWA 1005 External Wall Tiles (STK STW) WD 140 09-Nov-22 5d 03-May-23 50 S5OWA 1010 Artificial Wood Finish (STK STW) 150 04-May-23 31-Oct-23 166 7d WD S5OWA 1020 Aluminum Ceiling Cladding (STK STW) 3d WD 90 04-May-23 50 18-Aug-23 S5OWA 1030 Artificial Granite Tile (TSTP area) 60 31-Aug-23 11-Nov-23 156 3d WD S50WA 1040 Artificial Granite Tile (STK STW) 90 08-Dec-22 29-Mar-23 -71 3d WD S5OWA 1050 Fence and Gate for STK STW 84 06-Dec-23 19-Mar-24 52 3d WD S5OWA 1060 Completion of all Architectural Works 19-Mar-24 52 0dWD 10.8 Landscapi Landscaping Softworks at STW STW Roof and Wall S5OWL1000 36 30-Mar-23 16-May-23 -71 1d WD CD S5OWL1020 Establishment Works 365 17-May-23 15-May-24 10





# EXPANSION OF SHA TAU KOK SEWAGE TREATMENT WORKS PHASE 1 AND VILLAGE SEWERAGE IN TONG TO

Project ID :Mth Update_201906-1
Layout : Layout_TFP_2a
Page 10 of 10

Monthly Revised Programme (2019-06)							
Date Revision Checked Approve							
20-Jun-19	Rev 0	Justin C	Ron Hung				

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com




# Appendix B

**Project Organization Chart** 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



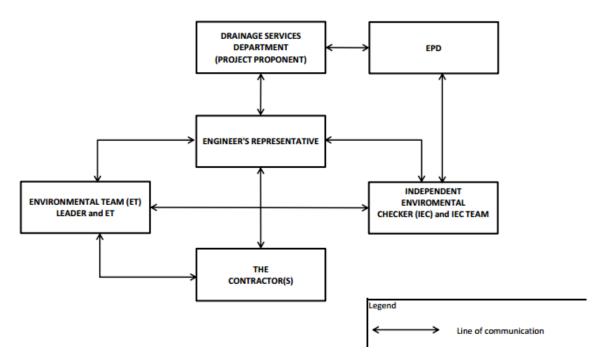

Note: Detailed key personnel contact names and telephone numbers refer to Table 1.1.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# Appendix C

**Calibration Certificates of Monitoring Equipment** 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



### www.casellasolutions.com



# Certificate of Conformity and Calibration

Instrument Model:- CEL-633A Serial Number 1488269

 Firmware revision
 V006-03

 Microphone Type: CEL-251
 Preamplifier Type: CEL-49

 Serial Number
 2869
 Serial Number
 004065

Instrument Class/Type:-

#### Applicable standards:-

IEC 61672; 2002 / EN 60651 (Electroacoustics - Sound Level Meters) IEC 60651 1979 (Sound Level Meters), ANSI S1.4: 1983 (Specifications For Sound Level Meters)

Note:- The test sequences performed in this report are in accordance with the current Sound level meter Standard - IEC61672. The combination of tests performed are considered to confirm the products electro-acoustic performance to all applicable standards including superceeded Sound Level Meter Standards - IEC60651 and IEC60604.

Test Conditions:-

30 °C 58 %RH 1003 mBar Test Engineer:-Date of Issue:- Chris Taylor September 7, 2018

#### Declaration of conformity:-

This test certificate confirms that the instrument specified above has been successfully tested to comply with the manufacturer's published specifications. Tests are performed using equipment traceable to national standards in accordance with Casella's ISO 9001:2008 quality procedures. This product is certified as being compliant to the requirements of the CE Directive.


### Test Summary:-

All Tests Pass Self Generated Noise Test Electrical Signal Test Of Frequency Weightings All Tests Pass All Tests Pass Frequency & Time Weightings At 1 kHz Level Linearity On The Reference Level Range All Tests Pass Toneburst Response Test All Tests Pass All Tests Pass C-peak Sound Levels All Tests Pass Overload Indication All Tests Pass Acoustic Tests

#### Combined Electro-Acoustic Frequency Response - A Weighted

Combined Electro-Acoustic Frequency Response - A Weighted (IEC 61672-3:2006)

The following A-Weighted frequency response graph shows this instruments overall frequency response based upon the application of multi-frequency pressure field calibrations. The microphones Pressure to Free field correction coefficients are applied to pressure response. Reference level taken at 1kHz.



Casella UK

Regent House, Wolfsley Road Kempston, Bedford MKA2 7.JV

Tel +44 (0) 1234 544100 Fax +44(0) 1234 541490 E-mai: wb@caselescuktors.c Casella USA

416 Lawtence Bell Cree, Unit 4 Buffett, NY 14221, USA TOR Free (600) 356-2966 Tel: +1 (716) 276-3040 Casella India

ldeal Industries India Pki Ltd. 229-230. Spazedge, Tower-B Solida Road, Sector-47. Gurgeon (22001, Hary via Linda Tet. +91. 124-449510. E-mail. control bares/Blobal-maisthes in Casella China

Ideal Industries China Room 305, Building 1, No 1379, Chuangai Rd, Pudong New Dirtied, Shanghai, China

Tel +86-21-31252188 Fac +85-21-61005806 Email Info@casetaloiutions on Casella Australia

Ideal Industries (Aust) PTV LTD Una 17, 35 Dunlop Rd, Mulgrave Vic. 3170, Australia

Email australo@casellass\unitare.zom

Tested to CEL-63X test sheet TP444 revision 01-00

Page 1 of

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



	CASELLA
	icate of nd Calibration for
CEL-120 Acou	ustic Calibrator
Applicable Standards :-IEC	60942: 2003 & ANSI S1.40: 2006
CEL-120/1 Class 1	
CEL-120/2 Class 2	
Serial No: 2393687	7
Firmwate: 04	
Temperature: 19 °C Pr	ressure: 1013 mb %RH 46
Frequency = 1.00kHz ± 2Hz T.H.D. = < 1%	Calibration Level
SPL @ 114.0dB Setting	11A-01 dB
SPL @ 94.0dB Setting (CEL-120/1 only)	93.97 dB/NA
Engineer :- Atte	Date :- 1 7 OCT 2018
	ng standards, used for conformance testing, are UK national standards, in accordance with the
Company test equipment and acoustic works subject to periodic calibration, traceable to company's ISO9	001 Quality System.
subject to periodic calibration, traceable to company's ISO9  DECLARATION  This certificate contirus that the instruments specifi	OF CONFORMITY  ed above has been produced and tested to comply with the relevant European Community CE directions.
subject in periodic calibration, traceable to company's ISO9  DECLARATION  This certificite confirms that the instrument specifi- the manufacturer's published specifications and  Regent Hurse, Wisheley Brade  Phone, +44 (8) 1234 844109	OF CONFORMITY of above has been produced and tested to comply with the relevant European Community CE directives.  ZEL (U.K.), L. Kempston, Bedfund, MK-32 TJY

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# Appendix D

**Environmental Monitoring Schedules** 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# Project: CM 8/2018 Expansion of Sha Tau Kok Sewage Treatment Works

Impact Monitoring Schedule (June 2019)

Sun	Mon	Tue	Wed	Thu	Fri	Sat
						1
2	3 Noise Impact Monitoring	4	5	6	7	8
9	10	11	12	13	14 Noise Impact Monitoring	15
16	17	18	19	20 Noise Impact Monitoring	21	22
23	24	25	26 Noise Impact Monitoring	27	28	29
30						

# Remarks

1. Noise Impact Monitoring at NM1 and NM2.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# Project: CM 8/2018 Expansion of Sha Tau Kok Sewage Treatment Works

Tentative Impact Monitoring Schedule (July 2019)

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2 Noise Impact Monitoring	3	4	5	6
7	8 Noise Impact Monitoring	9	10	11	12	13 Noise Impact Monitoring
14	15	16	17	18	19 Noise Impact Monitoring	20
21	22	23	24	25 Noise Impact Monitoring	26	27
28	29	30	31 Noise Impact Monitoring			

#### Remarks

- 2. Noise monitoring will be carried out at NM1 and NM2.
- 3. Actual monitoring schedule may be subjected to change due to any safety concern or adverse weather condition.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



# Appendix E

**Noise Monitoring Data and Graphical Presentations** 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail: matlab@fugro.com Website: www.fugro.com



# NM1 Block 45, Sha Tau Kok Chuen

		Measure	ed Noise Lev	el (MNL)	Baseline	Limit Level		Construction			
Date	Start Time	$L_{eq}^{*}$	L <sub>90</sub>	L <sub>10</sub>	(BNL)	Lillin Level	N	Noise Level (CNL)#		Remark	
		Unit: dB(A) 30 Mins					]				
03-Jun-19	14:24	65.0	51.0	62.5	65	75	65.0	Measured≦Baseline	Fine	-	
14-Jun-19	13:34	59.4	43.5	61.0	65	75	59.4	Measured≦Baseline	Fine	-	
20-Jun-19	10:35	68.0	62.5	70.5	65	75	65.0		Fine	-	
26-Jun-19	10:57	57.7	53.0	56.5	65	75	57.7	Measured≦Baseline	Cloudy	-	


**NM2** Building along Shun Lung Street


		Measure	ed Noise Lev	el (MNL)	Baseline	Limit Level		Construction		
Date	Start Time	L <sub>eq</sub> *	L <sub>90</sub>	L <sub>10</sub>	(BNL)	Lillin Level	N	loise Level (CNL)#	Weather	Remark
			Unit: dB(A) 30 Mins					]		
03-Jun-19	15:00	64.9	52.0	64.0	65	75	64.9	Measured≦Baseline	Fine	-
14-Jun-19	14:11	62.6	41.0	65.0	65	75	62.6	Measured≦Baseline	Fine	-
20-Jun-19	11:07	71.5	67.5	74.0	65	75	70.4		Fine	-
26-Jun-19	11:32	64.9	54.0	66.6	65	75	64.9	Measured≦Baseline	Cloudy	-

Note: \*Correction of +3dB(A) for Free-field Measurement. # CNL = 10 log  $(10^{MNL/10} - 10^{BNL/10})$ 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



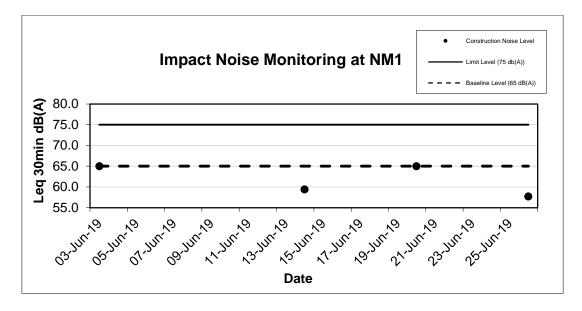

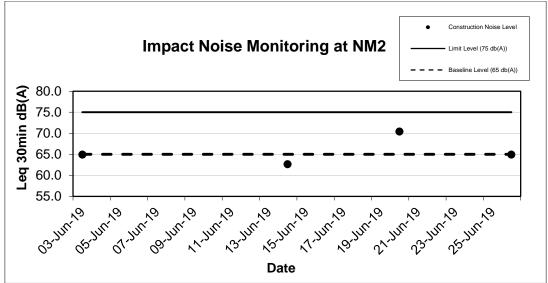

#### Note:

- 1) The QA/QC procedures and detection Limits refer to section 2.1 and 2.2.
- 2) The other factors influencing the monitoring results refer to section 2.5.6.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



## Appendix F

**Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions** 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



**Environmental Complaints Log** 

Complaint Log No.	Date of Complaint	Received From	Received By	Nature of Complaint	Investigation/Mitigation Action	Status
Nil	-	-	-	-	-	-

#### Remark:

**Cumulative Statistics on Complaints** 

Reporting Period	Complaints	Notifications of Summons	Successful Prosecutions
No. of Complaints , Notifications of Summons and Successful Prosecutions This Month	0	0	0
Cumulative Project-to-Date	0	0	0

**Cumulative Statistics on Monitoring Exceedance** 

Month/Year	No. of Exceedance				
Wionth/fear	Action	Limit			
No. of Exceedance This Month	0	0			
Cumulative Project-to-Date	0	0			

<sup>\*</sup> No Complaints, Notifications of Summons or Successful Prosecutions was received in the reporting period.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



Appendix G

**Site Audit Summary** 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



#### **Summary of Site Audit**

Inspection Date	Observation/ Comment	Follow Up Action	Completion Date
	Lock should be provided for Chemical Waste Cabinet.	Chemical Waste Cabinet was provided with lock.	05/06/2019
29/05/2019	Chemical stain should be removed with absorptive pads and treated as chemical waste. Leakage or hole of drip tray should be plugged.	The drip tray was plugged.	05/06/2019
	Reminder: - Chemical containers should be properly labelled Drip tray and label should be provided for Chemical container and used battery.	N.A	
05/06/2019	Reminder: - The Contractor was reminded to regularly clear up the debris on the access road to prevent dust nuisance to the surrounding.	Debris on the access road had been cleared up.	12/06/2019
12/06/2019	Reminder: - General rubbish at the entrance of site office should be dumped regularly to prevent over-loading of the rubbish container and attraction of rats NRMM label should be displayed and stuck with the air compressor Stagnant water should be removed from drip tray, and chemical containers should be stored inside the drip tray,	<ul> <li>General rubbish at the entrance of site office has been dumped.</li> <li>NRMM labels have been displayed.</li> <li>Stagnant water has been removed from drip tray. The empty chemical containers were removed from site.</li> </ul>	18/06/2019
	The Contractor was reminded to close the door of generator to minimize the noise emission.	The door of the Air Compressor had been closed for noise control.	26/06/2019
19/06/2019	The color of NRMM label of generator was faded out. The Contractor was reminded to use proper NRMM label.	Proper NRMM label had been provided & stuck to the generator.	26/06/2019
	Reminder: - Recycling bins were not found on site. The Contractor was reminded to place adequate recycling bins to encourage waste segregation and recycling.	Five colour recycle bins had been provided for waste segregation.	26/06/2019
26/06/2019	Drip tray should be provided for i) red chemical container on working site; & ii) Blue diesel drum at the entrance generator of site office.	Follow up action will be reported in the next reporting month.	

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



## Appendix H

**Events and Action Plan** 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



**Event and Action Plan for Construction Noise Monitoring** 

	Action Plan for Const	ACTION		
EVENT	ET	IEC	ER	Contractor
Action Level	1. Carry out investigation to identify the source and cause of the complaint/ exceedance(s) 2. Notify IEC, ER, and Contractor and report the results of investigation to the Contractor, ER and the IEC 3. Discuss with the Contractor and IEC for remedial measures required 4. If the complaint is related to the Project, conduct additional monitoring for checking mitigation effectiveness and report the findings and results to the IEC, ER and the Contractor	1. Review the analyzed results submitted by the ET. 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly. 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of Exceedance in writing. 2. Require Contractor to propose remedial measures for the analyzed noise problem. 3. Ensure remedial measures are properly implemented.	1. Submit noise mitigation proposals, if required, to the IEC and ER 2. Implement noise mitigation proposals
Limit Level	1. Carry out investigation to identify the source and cause of the exceedance 2. Notify IEC, ER, Project Proponent, EPD and Contractor 3. Repeat measurements to confirm findings 4. Provide investigation report to IEC, ER, EPD and Contractor of the exceedances 5. If the exceedance is related to the Project, assess effectiveness by additional monitoring. 6. Report the remedial action implemented and the additional monitoring results to IEC, EPD, ER and Contractor 7. If exceedance stops, cease additional monitoring	1. Review the analyzed results submitted by the ET 2. Discuss the potential remedial measures with ER, ET Leader and Contractor 3. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly 4. Supervise the implementation of remedial measures	1. Confirm receipt of notification of Exceedance in writing. 2. Require the Contractor to propose remedial measures for the analyzed noise problem. 3. Ensure remedial measures are properly implemented. 4. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor, in agreement with the Project Proponent, to stop that activity of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC and RE within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problem still not under control. 5. Stop the relevant activity of works as determined by the Project Proponent until the exceedance is abated.

Notes:

ET - Environmental Team, IEC - Independent Environmental Checker; ER = Engineering Representatives

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



#### Appendix I

Implementation Status of Environmental Mitigation Measures (Construction Phase)

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



EIA Ref	Objective & Address	Stage (D/C/O)	Recommended Environmental Protection Measures/ Mitigation Measures	Implementation Status in Construction Phase				
Air Quality								
			<ul> <li>Dust control measures stipulated in the Air Pollution Control (Construction Dust) Regulation shall be implemented during the construction of the Project to control potential fugitive dust emissions.</li> </ul>	۸				
			- Regular water spraying on exposed area.	٨				
			- Vehicle wheel-washing and body washing facilities shall be provided at the site entrance.	٨				
S3.7.1			<ul> <li>Shielding or covering with impervious sheet of stockpiled materials or exposed area when it is not used to reduce dust nuisance</li> </ul>	٨				
	Land site/	С	<ul> <li>Site practices such as regular maintenance and checking of the diesel-driven PMEs should be adopted to avoid any black smoke emissions and to reduce gaseous emissions</li> </ul>	٨				
	During Construction	C	<ul> <li>Open trench construction of the gravity sewers, each work front should be around 20m to 30m in length to control potential dust emission.</li> </ul>	N.O				
S3.6.1			The existing sewage pumping station and rising mains should be cleaned and flushed out properly to clear away any remaining potential sources of odour emission, such as sewage sludge from the facilities. The decommissioning including removal of the pumping station and rising mains should take place after the cleaning and flushing out.	۸				
S3.9.1			<ul> <li>Regular site inspections on a weekly basis shall be carried out in order to confirm that the mitigation and control measures are properly implemented and are working effectively to ensure proper control of construction dust and gaseous emissions.</li> </ul>	٨				
			Noise					
			- Use of quiet PME / quiet construction method	٨				
S4.8	Noise Control /	C	Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m-2 and have no openings or gaps.	N.O				
	During construction		<ul> <li>Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction phase;</li> </ul>	٨				
			<ul> <li>Silencers or mufflers on construction equipment should be utilised and properly maintained during the construction phase;</li> </ul>	٨				
			- Mobile plant, if any, should be sited as far away from NSRs as possible;	٨				

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.



EIA Ref	Objective & Address	Stage (D/C/O)	Recommended Environmental Protection Measures/ Mitigation Measures	Implementation Status in Construction Phase
			<ul> <li>Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum</li> </ul>	^
			<ul> <li>Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> </ul>	٨
			<ul> <li>Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities.</li> </ul>	N.O
			<ul> <li>The construction activities should be planned and carried out in sequence rather than simultaneously at each location. Therefore, only one unit of each type of equipment should be operated at any one time.</li> </ul>	۸
			<ul> <li>Open trench construction of the gravity sewers, each work front should be around 20m to 30m in length.</li> </ul>	N.O
S4.11	During construction	С	- Designated monitoring stations as defined in EM&A Manual/During construction phase	٨
	1		Water Quality	
\$5.9.2			<ul> <li>The trenchless HDD construction of outfall pipeline should proceed from the landside. Also, the construction of diffuser should be conducted after the dry excavation of marine sediment in the cofferdam.</li> </ul>	N.A
\$5.9.3	Marine Dredging/ During construction	С	<ul> <li>Furthermore, a number of standard measures and good site practices should be implemented to avoid / minimize the potential impacts from marine construction.         These measures include:         <ul> <li>All vessels should be well maintained and inspected before use to limit any potential discharges to the marine environment;</li> <li>All vessels must have a clean ballast system;</li> <li>No soil waste is allowed to be disposed overboard.</li> </ul> </li> </ul>	۸
\$5.9.3	Marine Dredging/ During construction	С	<ul> <li>No discharge of sewage/grey wastewater should be allowed. Wastewater from potentially contaminated area on working vessels should be minimized and collected. These kinds of wastewater should be brought back to port and discharged at appropriate collection and treatment system</li> </ul>	۸

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



EIA Ref	Objective & Address	Stage (D/C/O)	Recommended Environmental Protection Measures/ Mitigation Measures	Implementation Status in Construction Phase
			<ul> <li>General Construction Activities</li> <li>Standard site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" should be followed as far as practicable in order to reduce surface runoff, minimize erosion, and also to retain and reduce any SS prior to discharge.</li> </ul>	۸
			<ul> <li>Silt removal facilities such as silt traps or sedimentation facilities should be provided to remove silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities should be based on the guidelines provided in ProPECC PN 1/94.</li> </ul>	^
S5.9.4	Land site & drainage/	С	<ul> <li>All drainage facilities and erosion and sediment control structures should be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit should be removed regularly.</li> </ul>	۸
	During construction		- Earthworks to form the final surfaces should be followed up with surface protection and drainage works to prevent erosion caused by rainstorms.	^
			<ul> <li>Appropriate surface drainage should be designed and provided where necessary.</li> </ul>	۸
			<ul> <li>The precautions to be taken at any time of year when rainstorms are likely together with the actions to be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94.</li> </ul>	۸
			<ul> <li>Oil interceptors should be provided in the drainage system where necessary and regularly emptied to prevent the release of oil and grease into the storm water drainage system after accidental spillages.</li> </ul>	^
S5.9.4	Land site & drainage/ During construction	С	<ul> <li>Temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge, if any, should be adequately designed for the controlled release of storm flows. The temporary diverted drainage, if any, should be reinstated to the original condition when the construction work has finished or when the temporary diversion is no longer required.</li> </ul>	^
\$5.9.5	Land site & drainage/ During construction	С	<ul> <li>Appropriate infiltration control, such as cofferdam wall, should be adopted to limit groundwater inflow to the excavation works areas in the Project site. Groundwater pumped out from excavation area should be discharged into the storm system via silt removal facilities.</li> </ul>	N.O
S5.9.6	Land site & drainage/ During	С	<ul> <li>If needed, appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the construction workers over the construction site to prevent direct disposal of sewage into the water environment.</li> </ul>	۸

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.



EIA Ref	Objective & Address	Stage (D/C/O)	Recommended Environmental Protection Measures/ Mitigation Measures	Implementation Status in Construction Phase
\$5.9.7	construction		<ul> <li>Spillage of Chemicals</li> <li>Site drainage should be well maintained and good construction practices should be observed to ensure that oil, fuels, solvents and other chemicals are managed, stored and handled properly and do not enter the nearby streams or marine water.</li> </ul>	
S5.12.1	Marine Dredging/ During construction	O	<ul> <li>Marine water quality monitoring at selected WSRs is recommended for installation, maintenance and removal of sheetpile and sediment removal works under this Project. Site audit would also be conducted throughout the marine and land-based construction under this Project. Details environmental monitoring procedures and audit requirements are provided in the standalone EM&amp;A manual.</li> </ul>	
			Waste Management & Land Contamination	
S6.6.1	During construction	O	- An Environmental Management Plan (EMP) in accordance with ETWB TCW No. 19/2005 – "Environmental Management on Construction Sites" should be prepared by the main Contractor of each construction contract upon appointment. The EMP should describe the arrangements for avoidance, reduction, reuse, recovery, recycling, storage, collection, treatment and disposal of different categories of waste to be generated from the construction activities.	٨
S6.6.3	During construction	С	- An appropriate person, such as site agent or environmental officer should be nominated, to be responsible for good site practices, arrangement for collection and effective disposal of all wastes generated at the site to an approved facility. Training of construction staff should be undertaken by the Contractor about the concept of site cleanliness and appropriate waste management procedures. Requirements for staff training should be included in the EMP.	٨
S6.6.4	During construction	С	<ul> <li>Good planning and site management practices should be employed to eliminate over ordering or mixing of construction materials to reduce wastage. Regular cleaning and maintenance of the waste storage area should be provided.</li> </ul>	
\$6.6.5	During construction	О	<ul> <li>A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be implemented in accordance with DEVB TCW No. 6/2010. In order to monitor the disposal of C&amp;D materials and solid wastes at public fill reception facilities and landfills and to control fly-tipping, a trip-ticket system should be included.</li> </ul>	٨
S6.6.6	During construction	С	<ul> <li>Imported soft fill and rocks, if required, should be sourced from CEDD's fill bank, other projects or other approved sources instead of using new materials. Approval from the Engineer and all other relevant parties should be obtained by the Contractor before importation of the fill materials.</li> </ul>	NO

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



EIA Ref	Objective & Address	Stage (D/C/O)	Recommended Environmental Protection Measures/ Mitigation Measures	Implementation Status in Construction Phase
S6.6.7	During construction	С	<ul> <li>All waste materials should be segregated into categories covering:         <ul> <li>inert C&amp;D materials suitable for public filling facilities;</li> <li>recyclable materials / waste</li> <li>remaining non-inert C&amp;D materials for landfill;</li> <li>spent bentonite for public filling facilities;</li> <li>chemical waste; and</li> <li>general refuse for landfill</li> </ul> </li> </ul>	۸
S6.6.9	During construction	С	<ul> <li>Proper segregation and disposal of construction waste should be implemented. Separate containers should be provided for inert and non-inert wastes.</li> </ul>	٨
S6.6.11	During construction	С	- The reuse of inert C&D materials such as soil, rock and broken concrete should be maximised. Waste should be separated into fine, soft and hard materials.	٨
S6.6.12	During construction	С	<ul> <li>Prior to export of material from the site, the potential for it to be reused should be assessed. Most C&amp;D materials can easily be reused with minimum processing. Waste separation methods should be followed to ensure that C&amp;D waste is separated at source. Suitable soft materials should be used for landscaping and grading of embankments. Fine material should be separated out and used as topsoil.</li> </ul>	٨
S6.6.13	During construction	D&C	- Use of recycled aggregates whenever possible	٨
S6.6.14, S6.6.30	During construction	С	<ul> <li>All C&amp;D materials should be sorted on-site into inert and non-inert components by the Contractor.         Non-inert C&amp;D materials (C&amp;D waste) such as wood, glass and plastic should be reused and         recycled before disposal to a designated landfill as a last resort. Inert C&amp;D materials (public fill)         should be reused onsite or in other projects approved by relevant parties before disposed of at public         fill reception facilities. Steel and other metals if any should be recovered from C&amp;D materials and         recycled.</li> </ul>	۸
S6.6.15	During construction	С	<ul> <li>Good quality reusable topsoil should be stockpiled for later landscaping works. Stockpiles should be less than 2m in height, formed to a safe angle of repose and hydroseeded or covered with tarpaulin to prevent erosion during the rainy season and to minimise dust generation.</li> </ul>	N.O
S6.6.16	During construction	С	<ul> <li>Control measures for temporary stockpiles on-site should be taken in order to minimize the noise, generation of dust, pollution of water and visual impact.</li> </ul>	N.O
S6.6.17	During construction	С	The public fill to be disposed to public fill reception facilities must consist entirely of inert construction materials. Disposal of C&D waste to landfill must not have more than 50% by weight of inert material.	٨

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.



EIA Ref	Objective & Address	Stage (D/C/O)	Recommended Environmental Protection Measures/ Mitigation Measures	Implementation Status in Construction Phase
			The C&D waste delivered for landfill disposal should contain no free water and the liquid content should not exceed 70% by weight.	
S6.6.18	During construction	С	- In order to avoid dust or odour impacts, any vehicles leaving a works area carrying C&D waste or public fill should have their load covered up before leaving the construction site.	٨
\$6.6.20	During construction	O	With reference to the Sediment Quality Report in the EIA, only Category L sediment was identified. In accordance with ETWB TCW No. 34/2002, Type 1 – Open Sea Disposal should be adopted for the disposal of 3,040 m 3 excavated sediment during construction of the proposed outfall diffuser. The location of marine disposal site should be sought with MFC/CEDD. The Contractor shall obtain a Marine Dumping Permit in accordance with the Dumping at Sea Ordinance. The Contractor should provide separate submissions (e.g. Sediment Sampling and Testing Plan / Sediment Quality Report) to EPD / DASO authority when applying for the marine dumping permit under the Dumping at Sea Ordinance.	
S6.6.21	During construction	С	- Bentonite slurry used in the drilling works should be treated and recycled at the works area in STKSTW. Any bentonite that is not suitable for recycling should be suitably dewatered before disposed of at public fill reception facilities.	N.O
\$6.6.22 & \$6.6.37	During construction and operation	C & O	- Where the construction/ operation processes produce chemical waste, the Contractor must register with EPD as a chemical waste producer. Wastes classified as chemical wastes are listed in the Waste Disposal (Chemical Waste) (General) Regulation. These wastes are subject to stringent disposal routes. EPD requires information on the particulars of the waste generation processes including the types of waste produced, their location, quantities and generation rates. A nominated contact person must be registered with EPD.	۸
\$6.6.23 & \$6.6.37	During construction	С	<ul> <li>Storage, handling, transport and disposal of chemical waste should be arranged in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published by EPD, and should be collected by a licensed chemical waste collector.</li> </ul>	/
\$6.6.24 & \$6.6.37	During construction	С	Suitable containers should be used for specific types of chemical wastes, containers should be properly labelled (English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations), resistance to corrosion, safely stored and securely closed. Stored volume should not be kept more than 450 liters unless the specification has been approved by the EPD. Storage area should be enclosed by three sides by a wall, partition of fence that is at least 2 m height or height of tallest container with adequate ventilation and space.	۸
S6.6.25	During	С	- Hard standing, impermeable surfaces draining via oil interceptors should be provided in works	٨

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



EIA Ref	Objective & Address	Stage (D/C/O)	Recommended Environmental Protection Measures/ Mitigation Measures	Implementation Status in Construction Phase
& S6.6.37	construction		area compounds. Interceptors should be regularly emptied to prevent release of oils and grease into the surface water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain. Oil and fuel bunkers should be bunded and/or enclosed on three sides to prevent discharge due to accidental spillages or breaches of tanks. Bunding should be of sufficient capacity to accommodate 110% of the volume of the largest container or 20% of the total volume of waste, whichever is largest. Waste collected from any grease traps should be collected and disposed of by a licensed contractor.	
\$6.6.26 & \$6.6.37	During construction	С	<ul> <li>Lubricants, waste oils and other chemical wastes are likely to be generated during the maintenance of vehicles and mechanical equipment. Used lubricants should be collected and stored in individual containers which are fully labelled in English and Chinese and stored in a designated secure place. If possible, such waste should be sent to oil recycling companies, and the empty oil drums collected by appropriate companies for reuse or refill.</li> </ul>	۸
S6.6.27	During construction	С	<ul> <li>The registered chemical waste producer (i.e. the Contractor) has to arrange for the chemical waste to be collected by licensed collectors. The licensed collector should regularly take chemical waste to a licensed chemical waste treatment facility (such as the Chemical Waste Treatment Centre in Tsing Yi). A trip ticket system operates to control the movement of chemical wastes.</li> </ul>	۸
S6.6.28	During construction	С	<ul> <li>No lubricants, oils, solvents or paint products should be allowed to discharge into water courses, either by direct discharge, or as contaminants carried in surface water runoff from the construction site.</li> </ul>	^
S6.6.29	During construction	С	<ul> <li>All wooden materials used on-site should be kept separate from other wastes to avoid damage and to facilitate reuse. Timber which cannot be reused should be sorted out from other waste and stored separately from all inert waste before being disposed of to landfill.</li> </ul>	^
\$6.6.32	During construction	С	General refuse generated on-site should be stored in enclosed bins or skips and collected separately from other construction and chemical wastes and disposed of at designated landfill. A temporary refuse collection point should be set up by the Contractor at the works area to facilitate the collection of refuse by licensed waste collector. The removal of waste from the site should be arranged on a daily or at least on every second day by the Contractor to minimise any potential odour impacts, minimise the presence of pests, vermin and other scavengers and prevent unsightly accumulation of waste.	^
S6.6.33	During	С	- The recyclable component of the municipal waste generated by the workforce, such as	٨

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



EIA Ref	Objective & Address	Stage (D/C/O)	Recommended Environmental Protection Measures/ Mitigation Measures	Implementation Status in Construction Phase
	construction		aluminium cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.	
			Ecology	
			- Erect fences along the boundary of the works area before the commencement of works to prevent vehicle movements and encroachment of personnel onto adjacent areas.	٨
			<ul> <li>Regularly check the work site boundaries to ensure that they are not breached and that damage does not occur to surrounding areas.</li> </ul>	٨
S7.7.3	All area / During construction	С	<ul> <li>Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the surrounding habitats through proper management of waste disposal.</li> </ul>	٨
37.7.3		_	<ul> <li>To avoid/ minimise the potential disturbance on the Night Roosting Site for Great Egret if confirmed to be continuing their usage before the construction activities, major noisy works such as concrete breaking should not be undertaken within an area of 100m from the Night Roosting Site after 16:00 under normal working hours. (i.e. 16:00 to 07:00 of the following day).</li> </ul>	N.O
			- Strong artificial lighting should not be used in the area at night to avoid disturbance to the roosting ardeids.	N.O
			Landscape & Visual	
Table 9.6of EM&A Manual	To protect existing landscape resources during construction stage	С	<ul> <li>Preservation of Existing Vegetation: <ul> <li>Existing trees designated to be retained in-situ should be properly protected. Tree protection measures to be undertake shall be in accordance with DEVB TC(W) 7/2015 on "Tree Preservation" and Guidelines on Tree Preservation during Development" by DEVB. This may include the clear demarcation and fencing-off of tree protection zones, tight site supervision and monitoring to prevent tree damage by construction activities, and periodic arboricultural inspection and maintenance to uphold tree health. A total of around 108 nos. of trees should be retained in-situ within the tree survey area.</li> <li>Under current proposal, no tree is recommended to be transplanted since the trees in conflict with the proposed works are not suitable to be transplanted. However, should transplantation be proposed in the detailed design stage after an update tree survey, the recommended final recipient sites should be adjacent to their current locations. Enough time should be reserved for tree transplantation works to increase the survival rate of the transplanting trees. To ensure the</li> </ul> </li> </ul>	۸

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



Objective & Address		Recommended Environmental Protection Measures/ Mitigation Measures					
		survival of transplanted trees, protection work should be considered. The tree transplantation proposal shall be submitted to relevant authorities for approval together with the formal tree removal application. Tree transplanting works shall be undertaken in accordance with Guidelines on Tree Transplanting by DEVB.					
To reduce construction disturbance during construction stage	O	<ul> <li>Control of Site Construction Activities:</li> <li>Construction site controls shall be enforced, where possible, to ensure that the landscape and visual impacts arising from the construction phase activities are minimised. These construction site controls should include but not limited to the following: <ul> <li>Storage of materials should be carefully arranged to minimise potential landscape and visual impact.</li> <li>The location and appearance of site accommodation should be carefully designed to minimize potential landscape and visual impact.</li> <li>Site lighting should be carefully designed to prevent light spillage,</li> <li>Extent of the works area and construction period should be minimised as far as practicable.</li> <li>Screen hoarding with compatible design to blend into the surrounding natural environmental should be considered (Screen hoarding may not be practicable for works of upgrading existing rising mains due to the spatial constraints of the works area along the Shun Hing Street).</li> <li>Temporary works areas should be reinstated at the earliest possible opportunity.</li> </ul> </li> </ul>	٨				
To reduce landscape and visual impact during construction	D&C	<ul> <li>Colour of natural tones and non-reflective building materials shall be used for any outward facing building facades to avoid visual and glare disturbance</li> <li>Responsive lighting design         <ul> <li>Directional and full cut off lighting is recommended within the boundaries of STKSTW to minimise light spillage to the surroundings;</li> <li>Minimise geographical spread of lighting, only applying for safety at the key access points of the STKSTW; and</li> <li>Limited lighting intensity to meet the minimum safety and operation requirement.</li> </ul> </li> </ul>	^				
During	С	- Undertake trenchless excavation in the vicinity of the Tin Hau Temple and provide a buffer zone of	N.O				
	To reduce construction disturbance during construction stage  To reduce landscape and visual impact during construction	To reduce construction disturbance during construction stage  To reduce landscape and visual impact during construction  During  C	survival of transplanted trees, protection work should be considered. The tree transplantation proposal shall be submitted to relevant authorities for approval together with the formal tree removal application. Tree transplanting works shall be undertaken in accordance with Guidelines on Tree Transplanting by DEVB.  Control of Site Construction Activities:  - Construction site controls shall be enforced, where possible, to ensure that the landscape and visual impacts arising from the construction phase activities are minimised. These construction should include but not limited to the following:  - Storage of materials should be carefully arranged to minimise potential landscape and visual impact.  - The location and appearance of site accommodation should be carefully designed to minimize potential landscape and visual impact.  - Site lighting should be carefully designed to prevent light spillage,  - Extent of the works area and construction period should be minimised as far as practicable.  - Screen hoarding with compatible design to blend into the surrounding natural environmental should be considered (Screen hoarding may not be practicable for works of upgrading existing rising mains due to the spatial constraints of the works area along the Shun Hing Street).  - To reduce landscape and visual impact  To reduce landscape and visual impact and uppersonance (Screen hoarding may not be practicable for works of upgrading existing rising mains due to the spatial constraints of the works area along the Shun Hing Street).  - To reduce landscape and visual impact and uppersonance and visual impact and u				

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



EIA Ref	Objective & Address	Recommended Environmental Protection Measures/ Mitigation Measures	Implementation Status in Construction Phase
S10.3.51		- A condition survey and vibration impact assessment should be undertaken and if construction vibration monitoring and structural strengthening measures are required.	N.A
S10.3.52		<ul> <li>Vibration and settlement monitoring should also be undertaken during the construction works to ensure that safe levels of vibration are not exceeded, if it is recommended in the condition survey report.</li> </ul>	
S10.3.53		<ul> <li>If the maximum level is exceeded all works must stop and the structure must be examined to determine if it has been damaged. The contractor must also take measures, such as using smaller pneumatic drills to ensure that the levels are reduced to acceptable limits.</li> </ul>	
S10.3.54		If at any time during the construction period the foundation of the structure is affected by the works; the works shall be immediately suspended and the AMO notified. If the works cause any damage to the structures, the proponent should be responsible for the restoration and repair at their own cost. A method statement should be submitted to AMO for comment and the works should be under AMO's supervision.	N.O
S10.3.55		- Protective covering should be provided as an additional mitigation measure to the Tin Hau Temple.	N.O

Remarks: ^ Compliance of mitigation measure

/ Recommendation was made during site audit but not improved/ rectified by the Contractor in reporting period.

x Non-compliance of mitigation measure

N.A Not Applicable at this stage as no such site activities were conducted in the reporting period

N.O Not Observed during site inspection in the reporting period.

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



#### Appendix J

**Proactive Environmental Protection Proforma** 

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.



Reporting Period	Construction Works	Anticipated Impacts	Corresponding Mitigation Measures
27/05/2019	Piling Works in TSTP	Dust, Noise and water quality impact.	<ul> <li>All construction plants / machineries should be checked / serviced on a regular basis during the courses of construction to minimize the emission of noise generation and eliminate dark smoke emission.</li> <li>All C&amp;D materials generated should be transported and stored at temporary storage area. Cover should be provided during transportation of dusty materials. Suitable materials should be sorted for reuse on-site. Only non-inert C&amp;D material should be disposed off-site to NENT Landfill.</li> <li>All dump trucks should be equipped with mechanical covers to prevent the dust emission during transportation when necessary.</li> <li>Dust control measures, such as water spraying, should be provided during demolition works when necessary.</li> <li>Maintaining of wet surface on access road and keep slow speed in the site.</li> <li>Wastewater to be treated by wastewater treatment facilities before discharge.</li> <li>Conditions in the Environmental Permit and Discharge License should be followed.</li> <li>Fueling of equipment should be conducted carefully on-site by mobile tanker to avoid storage of fuel and oil spillage.</li> <li>Provision of drip trays for equipment likely cause spillage of chemical / fuel, and provide routine maintenance.</li> <li>Predict required quantity of concrete accurately and collect the unused fresh concrete at designated locations in the site for subsequent disposal.</li> <li>Provide sufficient mitigation measures as recommended in approved EIA Manual requirement.</li> </ul>

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong.



Coming Month	Construction Works	Anticipated Impacts	Corresponding Mitigation Measures
01/07/2019 - 31/07/2019	Piling Works in TSTP	Dust, Noise and water quality impact.	<ul> <li>All construction plants / machineries will be checked / serviced on a regular basis during the courses of construction to minimize the emission of noise generation and eliminate dark smoke emission.</li> <li>All C&amp;D materials generated will be transported and stored at temporary storage area. Cover will be provided during transportation of dusty materials. Suitable materials will be sorted for reuse on-site. Only non-inert C&amp;D material will be disposed offsite to NENT Landfill.</li> <li>All dump trucks will be equipped with mechanical covers to prevent the dust emission during transportation when necessary.</li> <li>Dust control measures, such as water spraying, will be provided during demolition works when necessary.</li> <li>Maintaining of wet surface on access road and keep slow speed in the site.</li> <li>Wastewater to be treated by wastewater treatment facilities before discharge.</li> <li>Conditions in the Environmental Permit and Discharge License should be followed.</li> <li>Fueling of equipment will be conducted carefully on-site by mobile tanker to avoid storage of fuel and oil spillage.</li> <li>Provision of drip trays for equipment likely cause spillage of chemical / fuel, and provide routine maintenance.</li> <li>Predict required quantity of concrete accurately and collect the unused fresh concrete at designated locations in the site for subsequent disposal.</li> <li>Provide sufficient mitigation measures as recommended in approved EIA Manual requirement.</li> </ul>

Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com Website : www.fugro.com



Appendix K

**Waste Flow Table** 

## Monthly Summary Waste Flow Table for 2019 (year)

Name of Person completing the record: <u>Justin Cheng (EO)</u>

Project: Expansion of Sha Tau Kok Sewage Treatment Works Phase 1 and Village Sewerage in Tong To

Contract No.: DC/2018/03

	Actual Quantities of Inert C&D Materials Generated Monthly							Actual Quantities of C&D Wastes Generated Monthly				
Month	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse	
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 m <sup>3</sup> )	
Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	
Feb	0.014	0.005	0.000	0.000	0.014	0.000	0.000	0.000	0.000	0.000	0.010	
Mar	0.017	0.000	0.000	0.000	0.017	0.000	0.000	0.000	0.000	0.000	0.009	
Apr	0.008	0.000	0.000	0.000	0.008	0.000	0.000	0.000	0.000	0.000	0.007	
May	0.022	0.000	0.000	0.000	0.022	0.000	0.000	0.000	0.000	0.000	0.007	
Jun	0.546	0.000	0.000	0.000	0.546	0.000	0.000	0.000	0.000	0.000	0.006	
Sub-total	0.607	0.005	0.000	0.000	0.607	0.000	0.000	0.000	0.000	0.000	0.039	
Jul												
Aug												
Sep												
Oct												
Nov												
Dec												
Total	0.607	0.005	0.000	0.000	0.607	0.000	0.000	0.000	0.000	0.000	0.039	

Notes:

- (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (2) Plastics refer to plastic bottles/containers, plastic sheets/ foam from packaging materials.
- (3) Broken concrete for recycling into aggregates.
