CONTRACT NO. SPW 25/2018

ENVIRONMENTAL TEAM FOR RELOCATION OF SHA TIN SEWAGE TREATMENT WORKS TO CAVERNS – SITE PREPARATION AND ACCESS TUNNEL CONSTRUCTION

UNDER ENVIRONMENTAL PERMIT NO. EP-533/2017

MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT

FEBRUARY 2020

CLIENTS: PREPARED BY:

Drainage Services Department

Lam Environmental Services Limited

11/F Centre Point 181-185 Gloucester Road, Wanchai, H.K.

Telephone: (852) 2882-3939
Facsimile: (852) 2882-3331
E-mail: info@lamenviro.com
Website: http://www.lamenviro.com

CERTIFIED BY:

Derek LO

Environmental Team Leader

DATE:

March 2020



AECOM Asia Co. Ltd. 13/F Grand Central Plaza, Tower 2 138 Shatin Rural Committee Road Shatin, Hong Kong

Attn: Mr. Simon Leung

Your Reference

Sha Tin Cavern Sewage Treatment Works

Our Reference EC/TC/BW/bw/T407129/

Correspondence/L040

3/F International Trade Tower 348 Kwun Tong Road Kowloon Hong Kong

T +852 2828 5757 F +852 2827 1823 mottmac.hk

Environmental Permit No. EP-533/2017

Contract No. DC/2018/05 Relocation of Sha Tin Sewage Treatment Works to **Caverns – Site Preparation and Access Tunnel Construction**

EP Condition 3.5 – Monthly EM&A Report for February 2020

12 March 2020

By Email

Dear Sir,

I refer to the letter dated 12 March 2020 (ref: LES/J2019-02/CS/L048) from the Environmental Team Leader certifying the captioned Monthly EM&A Report for February 2020.

I have no comment on the captioned report and hereby verify it as having complied with the requirements as set out in the EM&A Manual for the captioned project, in accordance with Condition 3.5 of Environmental Permit No. EP-533/2017.

Should you have any queries regarding the captioned or require any further information, please contact the undersigned at 2828 5875.

Yours faithfully for MOTT MACDONALD HONG KONG LIMITED



Brandon Wong Independent Environmental Checker T +852 2828 5875 Brandon.Wong@mottmac.com

Encl.

c.c. DSD

Lam Environmental Services Limited China State Joint Venture

Mr. Kenneth Poon

By Email

Mr. Derek Lo

By Email

Mr. F M Chung

By Email

TABLE OF CONTENTS

1	I	NTRODUCTION	6
	1.1 1.2	Scope of the ReportStructure of the Report	
2	P	ROJECT BACKGROUND	8
	2.1 2.2 2.3 2.4	Background	8 9
3	S'	TATUS OF REGULATORY COMPLIANCE	11
	3.1 3.2	Status of Environmental Licensing and Permitting under the Project Status of Submission under the EP- 533/2017	
4	MON	NITORING REQUIREMENTS	13
	4.1 4.2	Air Monitoring Noise Monitoring	
5.	MON	NITORING RESULTS	19
	5.1 5.2 5.3	Air Monitoring Results Noise Monitoring Results Waste Management	19
6.	COM	IPLIANCE AUDIT	21
	6.1 6.2 6.3 6.4	Air Monitoring Noise Monitoring Review of the Reasons for and the Implications of Non-compliance Summary of action taken in the event of and follow-up on non-compl	21 21
7.	ENV	IRONMENTAL SITE AUDIT	22
8.	COM	IPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION	23
9.	CON	ICLUSION	24



Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

LIST OF TABLES

Table 2.1	Schedule 2 Designated Projects under this Project
Table 2.2	Contact Details of Key Personnel
Table 3.1	Summary of the current status on licences and/or permits on environmental protection pertinent to the Project
Table 3.2	Summary of submission status for Contract no. DC2018/05 under EP-533/2017
Table 4.1	Air Monitoring Station
Table 4.2	Air Quality Monitoring Equipment
Table 4.3	Action and Limit Level for Air Quality Monitoring
Table 4.4	Noise Monitoring Station
Table 4.5	Noise Monitoring Equipment
Table 4.6	Action and Limit Level for Noise Monitoring
Table 5.1	Details of Waste Disposal for Contract no. DC/2018/05
Table 8.1	Cumulative Statistics on Complaints
Table 8.2	Cumulative Statistics on Successful Prosecutions
Table 9.1	Construction Activities and Recommended Mitigation Measures in Coming Reporting Month

LIST OF FIGURES

Figure 2.1	Project Layout
Figure 2.2	Project Organization Chart
Figure 4.1	Locations of Air Quality Monitoring Station
Figure 4.2	Locations of Noise Monitoring Station

LIST OF APPENDICES

Appendix 1.1	Ecological Monitoring Report
Appendix 3.1	Environmental Mitigation Implementation Schedule
Appendix 4.1	Action and Limit Level
Appendix 4.2	Copies of Calibration Certificates
Appendix 4.3	Wind data extracted from Sha Tin HKO Automatic Weather Station
Appendix 5.1	Monitoring Schedule for Reporting Month and Next Month
Appendix 5.2	Air Quality Monitoring Results and Graphical Presentations
Appendix 5.3	Noise Monitoring Results and Graphical Presentations
Appendix 5.4	Monthly Summary Waste Flow Table
Appendix 6.1	Event and Action Plans
Appendix 6.2	Summary for Notification of Exceedance
Appendix 8.1	Complaint Log
Appendix 9.1	Construction Programme of Individual Contracts

EXECUTIVE SUMMARY

- i. This is the Environmental Monitoring and Audit (EM&A) Monthly Report February of Relocation of Sha Tin Sewage Treatment Works to Caverns – Site Preparation and Access Tunnel Construction under Environmental Permit no. EP-533/2017 (Hereafter as "the Project"). This is the 12th EM&A report presenting the environmental monitoring findings and information recorded during the period of 1 February 2020 to 29 February 2020. The cut-off date of reporting is at the end of each reporting month.
- ii. In the reporting month, the principal work activities conducted are as follow:
 Contract no. DC/2018/05 Relocation of Sha Tin Sewage Treatment Works to Caverns Site
 Preparation and Access Tunnel Construction
 - Site Clearance
 - · Hand dig trial pit excavation
 - Root pruning and transplantation
 - Excavation for temporary haul road construction
 - Soil nail
 - Retaining wall construction
 - Piling works
 - Haul road construction
 - Noise barrier installation
 - Drainage works
 - Watermain installation
 - · Construction of Community Liaison Centre
 - Construction of steel bridge ramp
 - Tunnelling works

Air Quality Monitoring

- iii. 1-hour Total Suspended Particulates (TSP) monitoring would be conducted at five monitoring stations. The sampling frequency is 3 times in every 6 days.
- iv. Air quality monitoring for the stations AM1 and AM2 were commenced on 12 April 2019 while station AM5 was commenced on 18 April 2019. Air quality monitoring for the station AM4 was commenced on 3 May 2019. AM3(A) is under liaison for approval.
- v. No action or limit level exceedance was determined in the reporting period for the stations of AM1, AM2, AM4 and AM5.

Noise Monitoring

vi. Noise monitoring would be conducted at five noise monitoring stations once per week.



Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

- vii. Noise monitoring for stations CM4 and CM5 were commenced on 13 April 2019 and 18 April 2019 respectively. Noise monitoring for stations CM1 and CM3 were commenced on 2 May 2019. CM2(A) is under liaison for approval.
- viii. No action or limit level exceedance was determined in the reporting period for the stations of CM1, CM3, CM4 and CM5.

Site Inspections and Audit

- ix. The Environmental Team (ET) conducted weekly site inspections for the Contract on 5, 12, 19 and 27 February 2020. IEC attended the joint site inspection on 27 February 2020. No non-compliance was found during the site inspection.
 - Complaints, Notifications of Summons and Successful Prosecutions
- x. No environmental complaint was received in the reporting period.
- xi. No notification of summons and successful prosecutions was received in the reporting month.

Reporting Changes

- xii. The Ecological Monitoring Report is attached in the Appendix 1.1.
- xiii. Due to the project site closed with no scheduled site activities from 29 January to 2 February 2020, EM&A programme, including environmental site audit scheduled on 31 January 2020 and environmental monitoring scheduled on 29 January 2020 were suspended. The temporary suspension of construction phase EM&A programme was formally proposed by ET Leader on 25 Feb 2020, verified by IEC on 28 Feb 2020 and approved by EPD on 4 March 2020.

Future Key Issues

xiv. In coming reporting months, the scheduled construction activities and the recommended mitigation measures are listed as follows:

Key Construction Works Recommended Mitigation Measures Site clearance, noise barrier Dust control during dust generating works; installation and Community Liaison Implementation of proper noise pollution control; Centre, hand dig trial pit excavation, and excavation for temporary haul road Provision of protection to ensure no runoff out of construction, soil nail, retaining wall site area or direct discharge into public drainage construction, piling works, haul road system. construction, drainage works, Direct impact to plant species of conservation



Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

Key Construction Works	Recommended Mitigation Measures		
watermain installation, construction of	importance recorded in the vicinity of the		
steel bridge ramp and Tunnel works	construction sites shall be avoided		
	Excavation materials shall be well covered		
Root pruning and transplantation	Mitigation measures to dust and noise control		
	should be provided to construction of noise		
	barrier and Community Liaison Centre		



1 Introduction

1.1 Scope of the Report

- 1.1.1. Lam Environmental Services Limited (LES) has been appointed to work as the Environmental Team (ET) under Environmental Permit (EP) no. EP-533/2017 to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Relocation of Sha Tin Sewage Treatment Works to Caverns Site Preparation and Access Tunnel Construction (Register No.: AEIAR-202/2016).
- 1.1.2. In accordance with Clause 3.5 stated in EP-533/2017, 4 hard copies and 3 electronic copies of the Monthly EM&A Report shall be submitted to the Director within 2 weeks after the end of each reporting month throughout the entire construction period.
- 1.1.3. In accordance with Section 13.4.1.1 of the Project EM&A Manual, the Monthly EM&A Report should be prepared and submitted to the Contractor, the IEC, the ER and EPD within 10 working days at the end of each reporting month, with the first report due the month after construction commences.

1.2 Structure of the Report

- **Section 1** *Introduction* details the scope and structure of the report.
- **Section 2** *Project Background* summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.
- **Section 3** Status of Regulatory Compliance summarizes the status of valid Environmental Permits / Licenses during the reporting period.
- **Section 4** *Monitoring Requirements* summarizes all monitoring parameters, monitoring methodology and equipment, monitoring locations, monitoring frequency, criteria and respective event and action plan and monitoring programmes.
- **Section 5 Monitoring Results** summarizes the monitoring results obtained in the reporting period.
- **Section 6 Compliance Audit** summarizes the auditing of monitoring results, all exceedances environmental parameters.

Section 7 Environmental Site Audit – summarizes the findings of weekly site inspections undertaken within the reporting period, with a review of any relevant follow-up actions within the reporting period.

Section 8 Complaints, Notification of summons and Prosecution – summarizes the cumulative statistics on complaints, notification of summons and prosecution

Section 9 Conclusion

2 Project Background

2.1 Background

- 2.1.1. The Relocation of Sha Tin Sewage Treatment Works (STSTW) to Caverns (the Project) is implemented so as to release the existing site, of a size about 28 hectares, for other uses.
- 2.1.2. In May 2012, Drainage Services Department (DSD), the Project Proponent commenced a detailed feasibility study on "Relocation of Sha Tin Sewage Treatment Works to Caverns" (the Feasibility Study). The findings of Feasibility Study affirmed that relocating the STSTW to caverns to be constructed at Nui Po Shan of A Kung Kok is technically feasible and financially viable.
- 2.1.3. The Project is a Designated Project (DP) under the Environmental Impact Assessment Ordinance (EIAO). An application for an Environmental Impact Assessment (EIA) Study Brief under section 5(1)(a) of the EIAO was submitted on 12 May 2014 with a Project Profile (No. PP-508/2014) for the Project. An EIA Study Brief (No. ESB-273/2014) was issued in June 2014. An EIA for the Project was then undertaken, as part of the Assignment, in accordance with this EIA Study Brief and the Technical Memorandum on Environmental Impact Assessment Process (EIAO-TM). The location of the Project is shown Figure 2.1.

2.2 Scope of the Project and Site Description

2.2.1. The Project covers the following DP elements as specified in Schedule 2 of the EIAO (Cap.499), *Table 2.1* summarises the DPs under this Project.

Table 2.1 Schedule 2 Designated Projects under this Project

Item	Designated Project	EIAO Reference
DP1	Sewage treatment works with an installed capacity of more than 15,000 m3 per day under Item F.1	Schedule 2, Part I,
DP2	 Sewage treatment works under Item F.2 With an installed capacity of more than 5,000 m3 per day; and A boundary of which is less than 200m from the nearest boundary of an existing or planned residential area, educational institution and health care institution. 	Schedule 2 Part I
DP3	An activity for the reuse of treated sewage effluent from a treatment plant under Item F.4	Schedule 2 Part I

Contract No. SPW 25/2018 Environmental Team for Relocation of Sha Tin Sewage Treatment Works to Caverns – Site Preparation and Access Tunnel Construction

DP4	Underground rock caverns under Item Q.2	Schedule 2 Part I
DP5	An explosives depot in a stand-alone, purpose built building under Item K.10	Schedule 2 Part I;
DP6	Decommissioning of an explosives depot under Item 11	Schedule 2 Part II

2.3 Project Organization and Contact Personnel

- 2.3.1 Drainage Services Department is the overall project controllers for the Project. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.3.2 The proposed project organization and lines of communication with respect to environmental protection works are shown in <u>Figure 2.2.</u> Key personnel and contact particulars are summarized in *Table 2.2*:

Table 2.2 Contact Details of Key Personnel

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative	Chief Resident Engineer	Mr. Leung Chi Man, Simon	6393 8645	3914 5888
China State Joint		Site Agent	Mr. KONG Ming, Elvis	9186 2081	
Venture	Contractor	Environmental Officer	Ms. CHIU Mei Yu, Gloria	9224 2413	2672 2501
Mott MacDonald Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. Brandon Wong	2828 5875	2827 1823
Lam Environmental Services Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Derek Lo	2882 3939	2882 3331

2.4 Construction Activities

- 2.4.1 In the reporting month, the principal work activities conducted are as follow.
 - Site Clearance
 - Hand dig trial pit excavation

Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

- Root pruning and transplantation
- Excavation for temporary haul road construction
- Soil nail
- Retaining wall construction
- Piling works
- Haul road construction
- Noise barrier installation
- Drainage works
- Watermain installation
- Construction of Community Liaison Centre
- Construction of steel bridge ramp
- Tunnelling works
- 2.4.2 In coming reporting months, the scheduled construction activities are listed as follows:
 - Site Clearance
 - Hand dig trial pit excavation
 - Root pruning and transplantation
 - Excavation for temporary haul road construction
 - Soil nail
 - Retaining wall construction
 - Piling works
 - Haul road construction
 - Noise barrier installation
 - Drainage works
 - Watermain installation
 - Construction of Community Liaison Centre
 - · Construction of steel bridge ramp
 - Tunnel works

Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

3 Status of Regulatory Compliance

3.1 Status of Environmental Licensing and Permitting under the Project

3.1.1. A summary of the current status on licences and/or permits on environmental protection pertinent to the Project is shown in *Table 3.1*.

Table 3.1 Summary of the current status on licences and/or permits on environmental protection pertinent to the Project

Permits and/or Licences	Reference No.	Issued Date	Valid Period & Expiry Date (dd-MM-yyyy to dd-MM-yyyy)	Status
Notification of Works Under APCO	442872	7/3/2019	N.A.	Valid
Discharge Licence	WT00034319-2019	3/9/2019	30/9/2024	Valid
Billing account under Waste Disposal Ordinance	7033825	17/4/2019	N/A	Valid
Registration as a Chemical Waste Producer	5117-756-C4363-01	9/5/2019	N/A	Valid
Asbestos Abatement Licence				Nil
Construction Noise Permit	GW-RN0805-19	5/11/2019	7/11/2019 to 6/2/2020	Expired on 6 Feb 2020
Construction Noise Permit	GW-RN0935-19	17/12/2019	19/12/2019 to 18/2/2020	Expired on 18 Feb 2020
Construction Noise Permit	GW-RN0119-20	25/2/2020	27/2/2020 to 26/5/2020	Valid

3.2 Status of Submission under the EP- 533/2017

3.2.1. A summary of the current status on submission for Contract no. DC/2018/05 under EP-533/2017 is shown in *Table 3.2*.

Table 3.2 Summary of submission status for Contract no. DC2018/05 under EP-533/2017

EP Condition	Submission	Date of Submission	
Condition 1.12	Notification of Commencement Date of Works	18 February 2019	
Condition 2.1	Notification of EPD of Community Liaison Group	18 April 2019	



Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

EP Condition	Submission	Date of Submission
Condition 2.12	Management Organization of Main Construction Companies	18 April 2019
Condition 2.14	Submission of Detailed Vegetation Survey Report and Protection and Transplantation Proposal	18 April 2019
Condition 2.15	Submission of Detailed Woodland Compensation Plan	TBC
Condition 2.18	Submission of Landscape & Visual Mitigation and Tree Preservation Plan(s)	18 April 2019
Condition 2.2	Notification of EPD of telephone hotline	18 April 2019
Condition 2.22	Submission of Measures to Mitigate Traffic Noise from Ma On Shan Road	18 April 2019
Condition 3.1	Proposal for Commencement of Construction Phase Air Quality Monitoring in Phases	17 April 2019
Condition 3.1	Proposal for Alternative Sampling Method for Construction Phase Air Quality Monitoring (1-hr TSP)	16 April 2019
Condition 3.1	Proposal for Proposed Fine Adjustment for Air and Noise Monitoring Stations at Kowloon City Baptist Church Hay Nien Primary School & Updated EM&A Manual	6 March 2020
Condition 3.1	Temporary suspension of EM&A Programme during 29 Jan 2020 to 2 Feb 2020	28 February 2020
Condition 4.2	Dedicated internet website	22 May 2019

Contract No. SPW 25/2018 Environmental Team for Relocation of Sha Tin Sewage Treatment Works to Caverns – Site Preparation and Access Tunnel Construction

4 Monitoring Requirements

4.1 Air Monitoring

AIR QUALITY MONITORING STATIONS

- 4.1.1. Air monitoring stations AM1 and AM2 were setup and commencement of monitoring on 12 April 2019 while AM5 was setup and commencement of monitoring on 18 April 2019. Air quality monitoring for the station AM4 was commenced on 3 May 2019. AM3(A) is under liaison for approval, no monitoring for AM3(A) was conducted in the reporting period.
- 4.1.2. Based on the Project baseline report, the air quality monitoring station AM3, Ma On Shan Tsung Tsin Secondary School was relocated to AM3(A), Kowloon City Baptist Church Hay Nien Primary School.
- 4.1.3. Air quality monitoring station AM6 will commence at a later stage upon the commencement of the decommissioning and demolition of the existing Shatin Sewage Treatment Works. The proposal was verified by IEC and approved by EPD on 9 May 2019.
- 4.1.4. The air monitoring stations for the Project are listed and shown in *Table 4.1* and *Figure 4.1*.

Table 4.1 Air Monitoring Station

Monitoring Station	Monitoring Location	Level (in terms of no. of floor)
AM1	Ah Kung Kok Fishermen Village	G/F
AM2	Block H, Kam Tai Court	Roof
AM3(A)	Kowloon City Baptist Church Hay Nien Primary School	G/F (tentative)
AM4	Wellborn Kindergarten	G/F
AM5	The Neighbourhood Advice-Action Council Harmony Manor	Roof

AIR MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.1.5. One-hour TSP levels should be measured to indicate the impacts of construction dust on air quality.
- 4.1.6. The sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.
- 4.1.7. Portable direct reading dust meter was proposed to use for 1-hour TSP level instead of HVS to undertaking the air quality monitoring for the project at the stations of AM1, AM2, AM3(A), AM4 and AM5. The proposal was verified by IEC and submitted to EPD, the proposal has approved

Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

by EPD on 28 May 2019.

SAMPLING PROCEDURE AND MONITORING EQUIPMENT

4.1.8. Monitoring Procedures

- (a) Check the calibration period of portable direct reading dust meter prior to monitoring (The direct reading dust meter was calibrated at 2-years interval and checked with High Volume Sampler (HVS) yearly.)
- (b) Record the site condition near / around the monitoring stations.
- (c) Install the portable direct reading dust meter to the monitoring location.
- (d) Slide the power switch to turn the power on.
- (e) Check of portable direct reading dust meter to ensure the equipment operation in normal condition.
- (f) Select the period of measurement to 60mins.
- (g) Check and set the correct time.
- (h) Select the appropriate unit display for the equipment.
- (i) Slide the power switch to turn the power off when the monitoring period ended (3 times 1 hour TSP monitoring per day).
- (j) Uninstall the portable direct reading dust meter
- (k) Collected the sampled data for analysis.
- (I) Remark: Procedures (c) to (h) may be different subject to the brands and models of portable direct reading dust meter

4.1.9. Maintenance and Calibration

- (a) The direct reading dust meter was calibrated at 2-years interval and checked with High Volume Sampler (HVS) yearly to determine the accuracy and validity of the results measured.
- (b) Checking of direct reading dust meter will be carried out in order to determine the conversion factor between the direct reading dust meter and the standard equipment, HVS. The comparison check is to be considered valid based on correlation coefficient checked by HOKLAS laboratory.
- 4.1.10. The 1-hour TSP air quality monitoring was performed by using portable direct reading dust meters at each designated monitoring station. The brand and model of the equipment are given in **Table 4.2**.

Table 4.2 Air Quality Monitoring Equipment

Equipment	Brand and model
	Met One BT- 645
Portable direct reading dust meter	Met One AEROCET 831
	Hal Technology HAL-HPC301

Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

4.1.11. The calibration certificates of the air quality monitoring equipment are attached in <u>Appendix 4.2.</u> The calibration dates in the calibration certificates for portable direct reading dust meter models Met One BT-645 and Met One Aerocet 831 are presented in "month/day/year" format.

WIND DATA

4.1.12. The representative wind data from Sha Tin HKO Automatic Weather Station was obtained covering the 1-hr TSP monitoring periods. The wind data were extracted and shown in Appendix 4.3.

EVENT AND ACTION PLAN

4.1.13. The Action and Limit levels for construction air quality are defined in **Table 4.3** and <u>Appendix 4.1</u>. Should non-compliance of the air quality criteria occur, action in accordance with the Event and Action Plan in <u>Appendix 6.1</u> shall be carried out.

Table 4.3 Action and Limit Level for Air Quality Monitoring

Monitoring Locations	1-hour TSP Level in μg/m3	
	Action Level	Limit Level
AM1	294	500
AM2	325	500
AM3(A)	360	500
AM4	297	500
AM5	349	500

4.2 Noise Monitoring

NOISE MONITORING STATIONS

- 4.2.1. Noise monitoring stations CM4 and CM5 were setup and commencement of monitoring on 13 April 2019 and 18 April 2019 respectively. Noise monitoring for stations CM1 and CM3 were commenced on 2 May 2019. CM2(A) is under liaison for approval, no monitoring for CM2(A) was conducted in the reporting period.
- 4.2.2. Based on the Project baseline report, the noise monitoring station CM2, Ma On Shan Tsung Tsin Secondary School was relocated to CM2(A), Kowloon City Baptist Church Hay Nien Primary School.
- 4.2.3. The noise monitoring stations for the Project are listed and shown in *Table 4.4* and *Figure 4.2*.

Table 4.4 Noise Monitoring Station

Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

Monitoring Station ID	Monitoring Location	Measurement Type	Level (in terms of no. of floor)
CM1	Wellborn Kindergarten	Free field	G/F
CM2(A)	Kowloon City Baptist Church Hay Nien Primary School	Free field (tentative)	G/F (tentative)
CM3	S.K.H. Ma On Shan Holy Spirit Primary School	Façade	Roof
CM4	Ah Kung Kok Fishermen Village	Free field	G/F
CM5	The Neighbourhood Advice-Action Council Harmony Manor	Façade	Roof

NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.2.4. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
 - One set of measurements between 0700-1900 hours on normal weekdays;
 - One set of measurements between 1900-2300 hours;
 - One set of measurements between 2300-0700 hours of next day; and
 - One set of measurements between 0700-2300 hours on holidays (three consecutive Leq/5min readings).
- 4.2.5. If construction works are extended to include works during the hours of 1900-0700, additional weekly impact monitoring shall be carried out during evening and night-time works for the latter 3 sets of measurements specified in Section 4.1.2 above, one set of measurements shall at least include 3 consecutive Leq (5min) results.
- 4.2.6. Supplementary information for data auditing, statistical results such as L10 and L90 shall also be obtained for reference.
- 4.2.7. If a school exists near the construction activity, noise monitoring shall be carried out at the monitoring stations for the schools during the examination periods. The ET leader shall liaise with the school's personnel and the examination authority to ascertain the exact dates and times of all examination periods during the course of the contract.

MONITORING EQUIPMENT

4.2.8. Noise monitoring was performed using sound level meter at the designated monitoring locations. The sound level meters shall comply with the International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications. Acoustic calibrator shall be deployed to check the sound level meters at a known sound pressure level. Brand and model of the equipment is given in **Table 4.5**.

Table 4.5 Noise Monitoring Equipment

Equipment	Brand and Model
	NTi XL2
Integrated Sound Level Meter	B&K2236
	HONGLIM HLES-01
Acoustic Calibrator	Larson Davis CAL200

4.2.9. The calibration certificates of the noise monitoring equipment are attached in Appendix 4.2.

SAMPLING PROCEDURE AND MONITORING EQUIPMENT

4.2.10. Monitoring Procedure

- (a) The monitoring station shall normally be at a point 1m from the exterior of the sensitive receiver's building façade and be at a position 1.2m above the ground.
- (b) Façade measurements were made at the monitoring locations. For free-field measurement, a correction factor of +3 dB (A) would be applied.
- (c) The battery condition was checked to ensure the correct functioning of the meter.
- (d) Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
- (e) Frequency weighting: A, Time weighting: Fast, Measurement time set: continuous 5 mins
- (f) Prior and after to the noise measurement, the meter was checked using the acoustic calibrator for 94dB (A) at 1000 Hz. If the difference in the calibration level before and after measurement was more than ±1 dB (A), the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.
- (g) Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

4.2.11. Maintenance and Calibration

- (a) The microphone head of the sound level meter was cleaned with soft cloth at regular intervals.
- (b) The sound level meter and calibrator were calibrated at yearly intervals.

EVENT AND ACTION PLAN

4.2.12. Noise Standards for Daytime Construction Activities are specified under EIAO-TM. The

Contract No. SPW 25/2018 Environmental Team for Relocation of Sha Tin Sewage Treatment Works to Caverns – Site Preparation and Access Tunnel Construction

Action and Limit levels for construction noise are defined in **Table 4.6** and **Appendix 4.1**. Should non-compliance of the criteria occurs, action in accordance with the Event and Action Plan in **Appendix 6.1** shall be carried out.

Table 4.6 Action and Limit Level for Noise Monitoring

		Limi	t Level (dB(A))	
Monitoring Station	Action Level	0700-1900 hrs on normal weekdays	0700-2300 hrs on holidays (including Sundays); and 1900-2300 hrs on all days ²	2300-0700 hrs of all days ²
CM1		65 / 70 ¹		
CM2(A)	When one documented	65 / 70 ¹		
CM3	complaint is	65 / 70 ¹	60 / 65 / 70 ³	45 / 50 / 55 ³
CM4	received	75		
CM5		75		

- Remark 1: Limit level of CM1, CM2(A) and CM3 reduce to 65 dB (A) during examination periods if any.
- Remark 2: Construction noise during restricted hours is under the control of Noise Control Ordinance Limit Level to be selected based on Area Sensitivity Rating.
- Remark 3: Limit Level for restricted hour monitoring shall act as reference level only. Investigation would be conducted on CNP compliance if exceedance recorded during restricted hour noise monitoring period.

Contract No. SPW 25/2018 Environmental Team for Relocation of Sha Tin Sewage Treatment Works to Caverns – Site Preparation and Access Tunnel Construction

5. Monitoring Results

- 5.0.1 The environmental monitoring will be implemented based on the division of works areas of each designed projects. Overall layout showing work areas and monitoring stations is shown in Figure 2.1 and Figure 4.1 4.2 respectively.
- 5.0.2 The environment monitoring schedules for reporting month and coming month are presented in **Appendix 5.1**.

5.1 Air Monitoring Results

- 5.1.1 1-hour TSP monitoring was conducted at AM1, AM2, AM4 and AM5 in the reporting month. No 1-hour TSP monitoring was scheduled at AM3(A) due to approval of monitoring station is still under liaison.
- 5.1.2 No action or limit level exceedance was determined in the reporting period at stations of AM1, AM2, AM4 and AM5
- 5.1.3 Air quality monitoring results measured in this reporting period for AM1, AM2, AM4 and AM5 are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in <u>Appendix 5.2.</u>

5.2 Noise Monitoring Results

- 5.2.1 Noise monitoring was conducted at CM1, CM3, CM4 and CM5 in the reporting month. No noise monitoring was scheduled at CM2(A) due to approval of monitoring station is still under liaison.
- 5.2.2 No action or limit level exceedance was determined in the reporting period at stations of CM1, CM3, CM4 and CM5.
- 5.2.3 Noise monitoring results measured in this reporting period for CM1, CM3, CM4 and CM5 are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in <u>Appendix 5.3</u>.

5.3 Waste Management

5.3.1 The quantities of waste for disposal in the Reporting Period are summarized in **Table 5.1**. The Monthly Summary Waste Flow Table is shown in <u>Appendix 5.4</u>. Whenever possible, materials were reused on-site as far as practicable.

Table 5.1 Details of Waste Disposal for Contract no. DC/2018/05

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials	391	2435	Fill Bank at Tuen Mun Area 38
disposed, m ³	14049	21940	Tai Po Area 9 under HKHA's Contract No.20160310 (Alternative Disposal Ground)
Inert C&D materials recycled, m ³	38	147	Fill Bank at Tuen Mun Area 38
Non-inert C&D materials disposed, tonne	78.23	364.66	NENT
Non-inert C&D materials recycled, kg	0	0	
Chemical waste disposed,	320	320	Collected by licensed chemical collector_ Ecospace Limited
Asbestos waste disposed, Kg	0	0	



Contract No. SPW 25/2018 Environmental Team for Relocation of Sha Tin Sewage Treatment Works to Caverns – Site Preparation and Access Tunnel Construction

6. Compliance Audit

- 6.0.1. The Event Action Plan for construction noise, air quality are presented in Appendix 6.1.
- 6.0.2. The summary of exceedance is presented in **Appendix 6.2**.

6.1 Air Monitoring

6.1.1 No action or limit level exceedance was determined in the reporting period at stations of AM1, AM2, AM4 and AM5. No 1hr TSP monitoring was scheduled at stations of AM3(A) due to approval of monitoring station is still under liaison.

6.2 Noise Monitoring

- 6.2.1 No action or limit level exceedance was determined in the reporting period at stations of CM1, CM3, CM4 and CM5, No noise monitoring was scheduled at stations of CM2(A) due to approval of monitoring station is still under liaison.
- 6.3 Review of the Reasons for and the Implications of Non-compliance
- 6.3.1 No environmental non-compliance was recorded in the reporting month.
- 6.4 Summary of action taken in the event of and follow-up on non-compliance
- 6.4.1 There was no particular action taken since no non-compliance was recorded in the reporting period.

Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

7. Environmental Site Audit

7.0.1. Within this reporting month, weekly environmental site audits were conducted on 5, 12, 19 and 27 February 2020. IEC attended the joint site inspection on 27 February 2020.

Table 7.1 Summary of Environmental Inspections for Contract no. SPW 25/2018

Item	Date	Reminders/Observations	Action taken by Contractor	Outcome
20200205_01Env	5-2-2020	Portion 11: The loosely surface should be covered	Loos covered properly	Completed by contractor on 6
		properly	property	Feb 2020
20200212_01Env	12-2-2020	Portion 2: Dusty stockpile should be covered or spray		Completed by contractor on 13
		with water	arranged to water the dusty stockpile regularly	Feb 2020

7.0.2. Within this reporting month, bi-weekly landscape site audits were conducted on 12 and 27 February 2020.

Table 7.2 Summary of Landscape Inspections for Contract no. SPW 25/2018

Item	Date	Reminders/Observations	Action taken by Contractor	Outcome
Nil	Nil	Nil	Nil	Nil

7.0.3. Within this reporting month, monthly ecology site audits were conducted on 20 February 2020.

Table 7.3 Summary of Ecology Inspections for Contract no. SPW 25/2018

Item	Date	Reminders/Observations	Action taken by Contractor	Outcome
20200220_01Eco	20/2/2020	Portion 11: Flower buds is Keep in view Keep in v		Keep in view
		observed in H001		

8. Complaints, Notification of Summons and Prosecution

- 8.0.1. No notification of summons and successful prosecutions was received in the reporting month.
- 8.0.2. The details of cumulative complaint log and updated summary of complaints are presented in Appendix 8.1.
- 8.0.3. Cumulative statistic on complaints and successful prosecutions are summarized in **Table 8.1** and **Table 8.2** respectively.

Table 8.1 Cumulative Statistics on Complaints

Reporting Period	No. of Complaints
February 2020	0
Total	1

Table 8.2 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative No. Project-to-Date
Air	-	0	0
Noise	-	0	0
Waste	-	0	0
Total	-	0	0

Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin
Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

9. Conclusion

- 9.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.
- 9.0.2. The scheduled construction activities and the recommended mitigation measures for the coming month are listed in **Table 9.1**. The construction programmes of the Project are provided in **Appendix 9.1**.

Table 9.1 Construction Activities and Recommended Mitigation Measures in Coming Reporting Month

Key Construction Works	Recommended Mitigation Measures
Site clearance, noise barrier installation and Community Liaison Centre, hand dig trial pit excavation, excavation for temporary haul road	 Dust control during dust generating works; Implementation of proper noise pollution control; and Provision of protection to ensure no runoff out of
construction, soil nail, retaining wall construction, piling works, haul road construction, drainage works, watermain installation, construction of steel bridge ramp and Tunnel works	 site area or direct discharge into public drainage system. Direct impact to plant species of conservation importance recorded in the vicinity of the construction sites shall be avoided
Root pruning and transplantation	 Excavation materials shall be well covered Mitigation measures to dust and noise control should be provided to construction of noise barrier and Community Liaison Centre

Figure 2.1

Project Layout

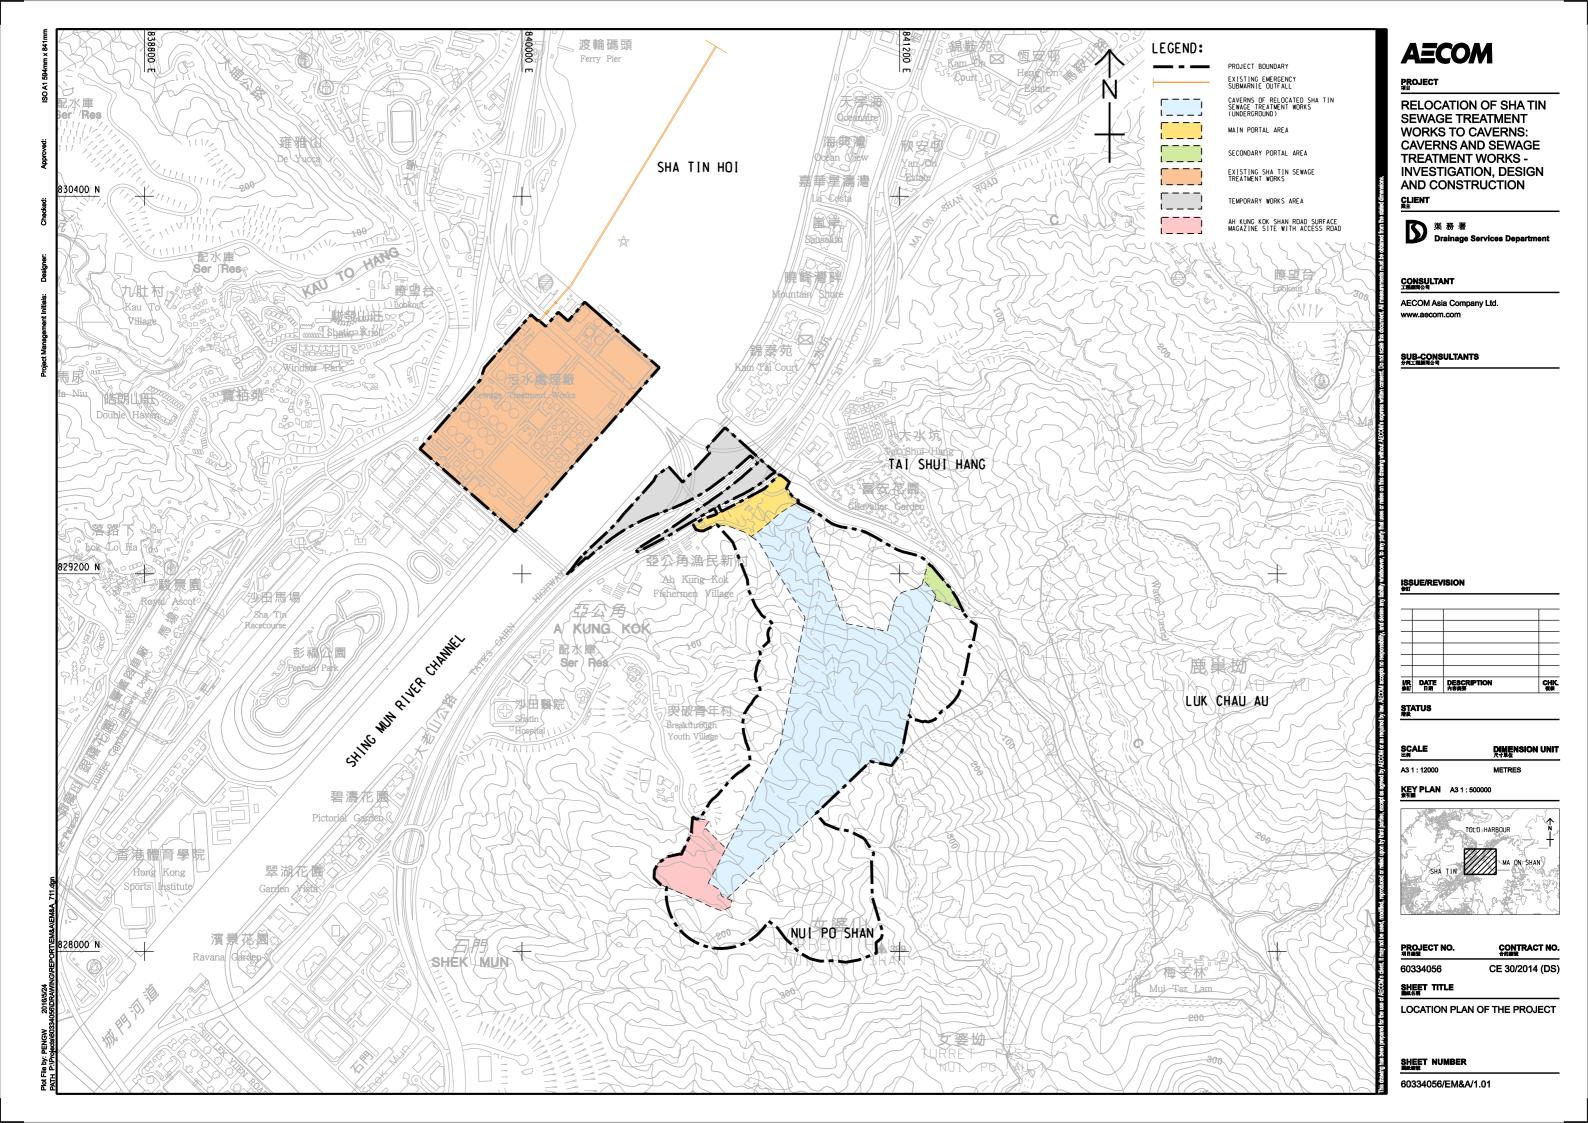


Figure 2.2

Project Organization Chart

Project Organization Chart



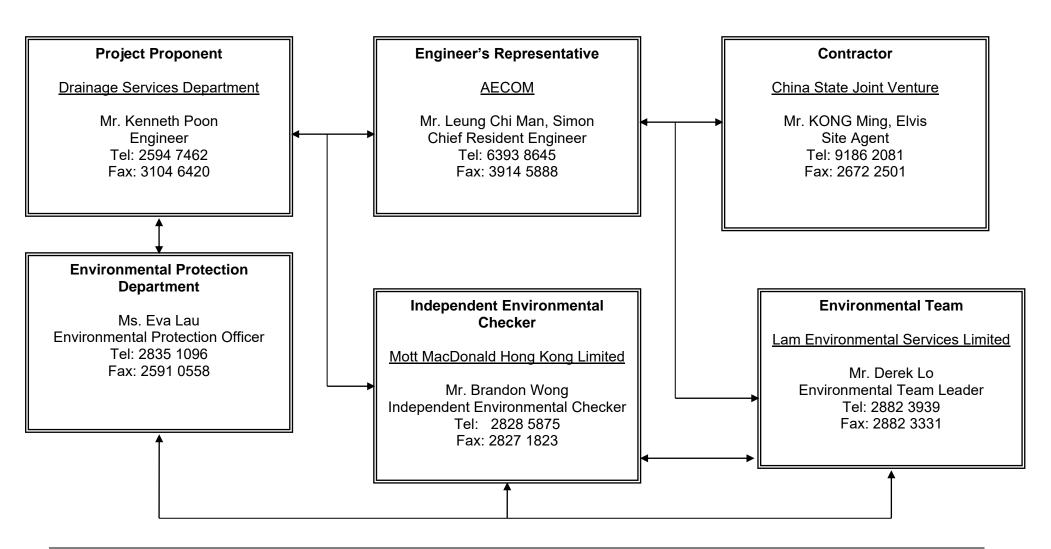


Figure 4.1 to Figure 4.2

Locations of Monitoring Stations

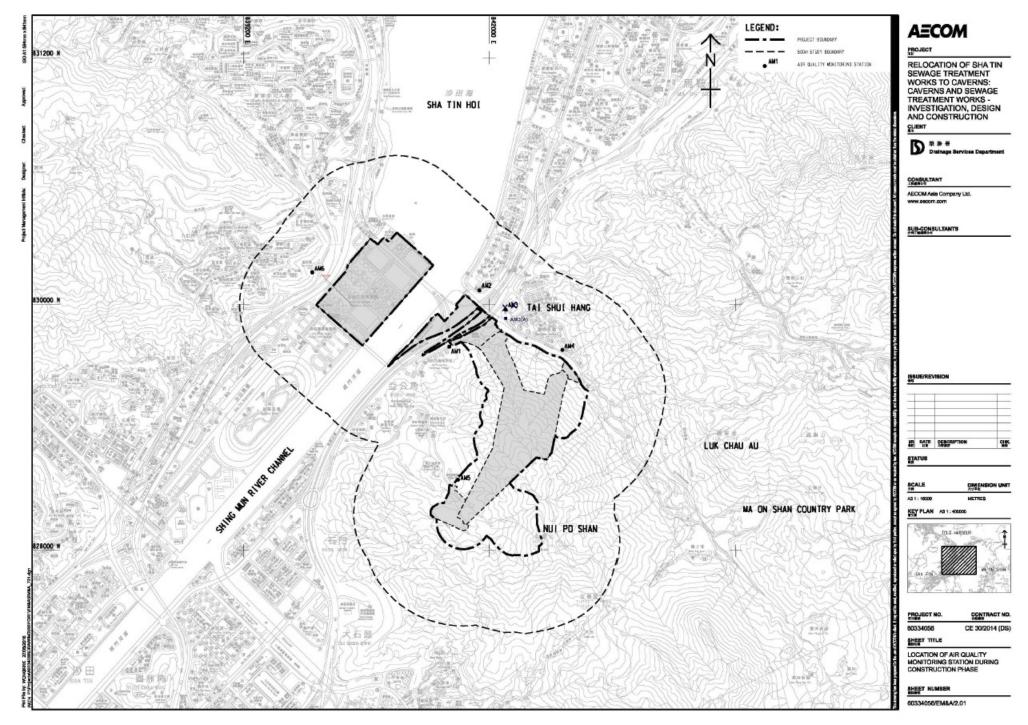

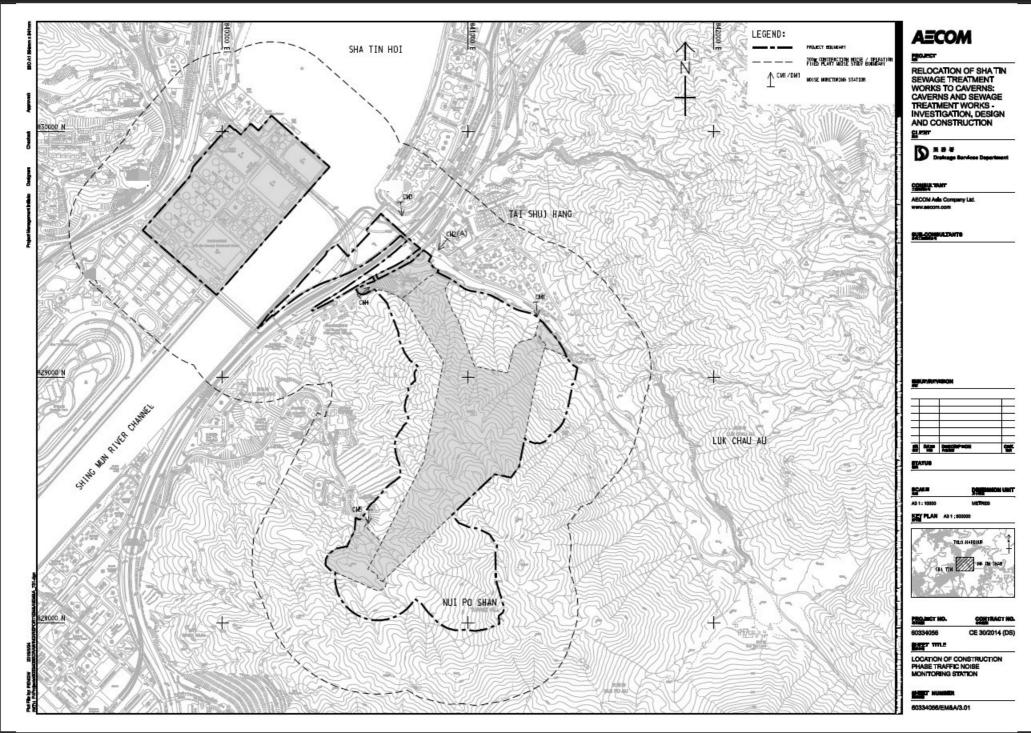

Appendix 1.1 Ecological Monitoring Report

CONTRACT NO. SPW 25/2018

ENVIRONMENTAL TEAM FOR RELOCATION OF SHA TIN SEWAGE TREATMENT WORKS TO CAVERNS – SITE PREPARATION AND ACCESS TUNNEL CONSTRUCTION

UNDER ENVIRONMENTAL PERMIT NO. EP-533/2017

8th ECOLOGICAL MONITORING REPORT FEBRUARY 2020

TABLE OF CONTENTS

1. Recommendation on plant species of conservation importance under approved	
protection and transplantation proposal	3
2. Ecological monitoring	3
2.1 Pre-construction survey	3
2.2 Transplantation	3
2.3 One-year Establishment Period after Planting (Post-Transplantation Monitoring)	4
2.4 Bi-weekly Ecological Monitoring	5
FIGURES	6
Figure 1	6
Figure 2	7
Figure 3	8
Figure 4	9
PLATE	. 10
Plate 1	. 10
TABLE	.11
Table 1	. 11
Table 2	. 13
Table 3	. 15
Appendix 1	. 16
Appendix 2	. 27
Appendix 3	. 29

1. RECOMMENDATION ON PLANT SPECIES OF CONSERVATION IMPORTANCE UNDER APPROVED PROTECTION AND TRANSPLANTATION PROPOSAL

According to the approved Protection and Transplantation Proposal, four out of six recorded plant species of conservation importance are to be transplanted. They were summarized in **Table 1**.

2. ECOLOGICAL MONITORING

2.1 Pre-construction survey

As per Section 3.1 of the approved Protection and Transplantation Proposal, pre-construction survey shall be carried out by a qualified ecologist which includes: -

- (1) Desktop study and survey preparation based on the specific area of site clearance as notified by the construction contractor and confirmed with the Resident Site Staff;
- (2) Schedule and conduct physical site survey to locate the affected species, reconfirm the species condition and record the physical condition before transplantation; and
- (3) Report site survey results and provide recommendations to contractor on transplantation and post-transplantation maintenance.

Pre-construction survey implementation

For the reporting month, there was no pre-construction survey according to work progress notified by the construction contractor.

2.2 Transplantation

Based on method statement in the approved Protection and Transplantation Proposal, transplantation works of the 1st batch of *Diospyros vaccinioides* (40 nos. of individuals) were commenced on 3 Aug 2019. The 2nd batch of *Diospyros vaccinioides* (228 nos. individuals) at Portion 12 of Site 1 were commenced on 17 Feb 2020 by the Landscape Specialist Contractor. Both actions did not require onsite monitoring from ET's Ecologist as agreed. They were temporarily stored and kept at the nursery before being transplanted to designated planting area at Site 3.

Another 140 individuals that not suitable for transplantation was still retained at Portion 12 of Site 1.

<u>Transplantation implementation</u>

The 1st batch of *Diospyros vaccinioides* transplantation involved 40 nos. of individuals originated from Site 1 (named as DV0001-DV0040) (**Figure 1**).

The 2nd batch of *Diospyros vaccinioides* transplantation involving 228 nos. of individuals is in progress during the reporting period.

The nursery is an open cleared wasteland within Site 2 (**Figure 2**), a shelter was erected for the transplanted *Diospyros vaccinioides* against environmental stress. Each plant was tagged and lined up in rows. Water supply is ready for irrigation (**Plate 1**).

There was no construction activity during the reporting month at/ around the nursery.

2.3 One-year Establishment Period after Planting (Post-Transplantation Monitoring)

Regular monitoring of health condition of transplanted plants, also called post-transplantation monitoring, should be carried out in monthly basis in the first three months, quarterly afterwards during one-year establishment period after transplanting to receptor site/ nursery as per Section 5.4 and 5.5 of the approved Protection and Transplantation Proposal.

Post-transplantation monitoring implementation

Post-transplantation monitoring for *Diospyros vaccinioides* (DV0001-DV0040) and *Ania hongkongensis* (named as H0002) were conducted on 5 February 2020 at their corresponding receptor sites/ nursery (**Figure 2 and Figure 3**). Extra monitoring effort fon them was made on 20 February 2020.

Monitoring for 1 no. of *Aquilaria sinensis* seedling (named as C0001) and 7 nos. of *Cibotium barometz* (grouped as E0004) will be conducted on a quarterly basis and the coming monitoring will be carried out in March 2020 (**Figure 4**).

Post-transplantation monitoring findings

Plant conditions of DV0001-DV0040 were listed in **Table 2**. Most seedlings were generally tiny (about 10cm in height) aiming at smaller root zone and better survival. However, some of them have yet developed sufficient leaves. Sign of leaf drop and dehydration has been observed (**Plate 1**), despite provision of shelter and irrigation. Although tiny new branch or leaf buds were observed, seedlings may struggle for survival against environmental stress.

Until 20 February 2020, 38% (15 out of 40 individuals) of transplanted seedlings has died or turned in poor condition, as illustrated in **Appendix 1**.

For C0001, E0004 and H0002, plant conditions were listed in **Table 3**, and corresponding photographic records were shown in **Appendix 2**. Despite root balls were maintained intact as far as possible, transplanted plants need time to grow into new soil of the receptor site. Therefore, sign of dehydration, leaf yellowing/ wilting, or even die-off were expected.

Meanwhile, it is observed that site clearance was carried out in the continue patch of woodland surrounding receptor sites of H0002. A shelter has been set up for the transplanted plants to provide similar shading against adverse environmental condition (e.g. strong sunlight, rainstorm and construction dust). Next few monitoring would be important to access their progress of recovery and establishment of new root system at the receptor site. In addition, it is observed that organic soil conditioner was applied by the Contractor to H0002 in order to retain water moisture in the soil.

Recommendation on post-transplantation monitoring maintenance

According to environmental condition and location of the receptor sites/ nursery, watering frequency was recommended in daily practice for at least the first 3 months as the transplant time is in summer months with strong sunlight and high temperature; except the days with fog and rain. Water frequency may be reduced based on the plant condition after monitoring in the first 3 months.

In contrast, the Landscape Contractor was recommended to check all transplanted plants after heavy rains/ typhoon under safe condition, in order to carry out any stabilization/ maintenance work. Blocked drainage shall be cleared; excessive water shall be pumped or diverged from nursery ground; saturated soil shall be aerated.

Other maintenance works (e.g. weeding, spraying off construction dust, use of approved pesticide and fertilization) shall be determined throughout the monitoring period in agreement with the Supervisor of the Contract and ET.

2.4 Bi-weekly Ecological Monitoring

According to Section 6.4 of the approved Protection and Transplantation Proposal, regular ecological site inspection should be carried out at least once every two weeks during the construction period.

Bi-weekly ecological monitoring implementation

Bi-weekly ecological monitoring was carried out on 5 and 20 February 2020 in the reporting month.

Bi-weekly ecological monitoring findings

The patch of retained *Ania hongkongensis* (named as H0001) was observed in a fair condition during reporting period. Flower buds were observed from the individuals of *Ania hongkongensis* with corresponding photos presented in **Appendix 3**. The protection zone of H0001 has been expanded due to additional individuals were observed. Mulch has been added for transplanted H0002.

FIGURES

Figure 1. Original location of DV0001-DV0040 at Site 1 to be transplanted to the nursery.

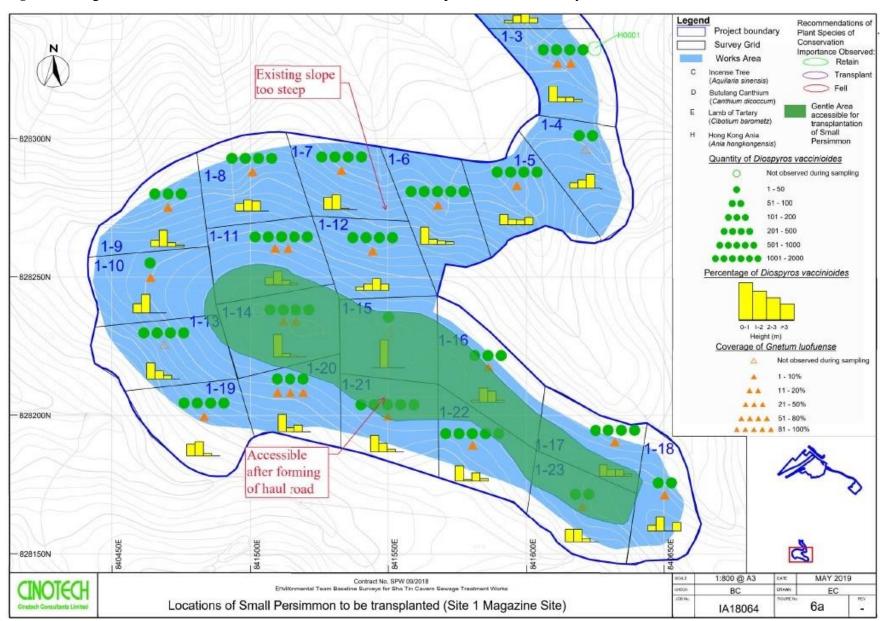


Figure 2. Nursery site highlighted in red frame for DV0001-DV0040 at Site 2.

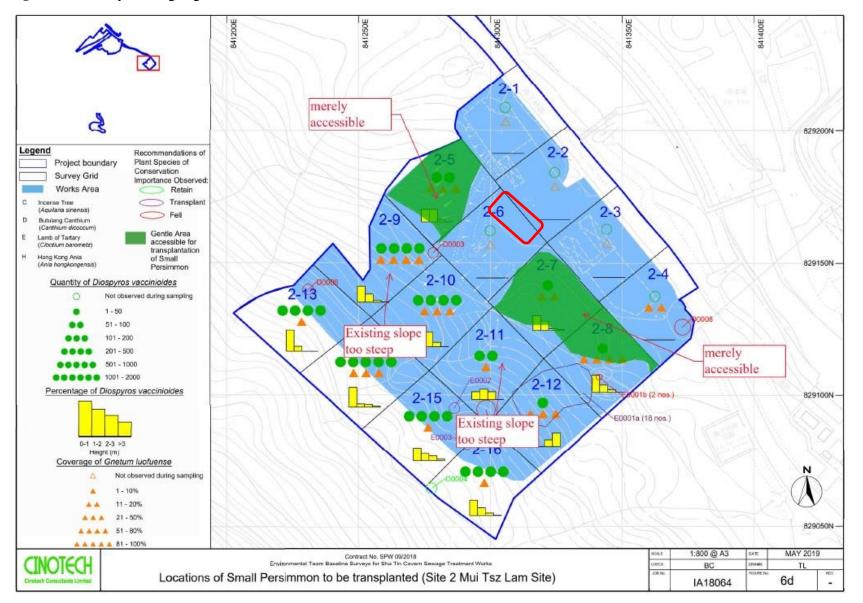


Figure 3. Original location of H0002 highlighted in yellow frame and its receptor site highlighted in red frame.


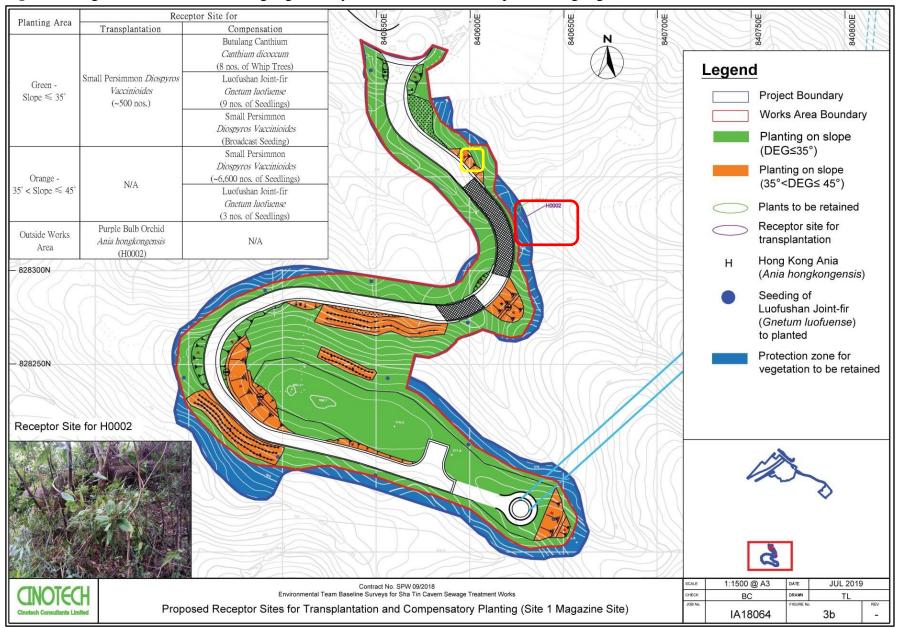


Figure 4. Receptor site for C0001 and E0004, the area highlighted in red frame is enlarged.



PLATE

Plate 1. The 1st batch of 40 nos. and the 2nd batch of *Diospyros vaccinioides* transplanted from Site 1; stored by Landscape Specialist Contractor at the on-site nursery.

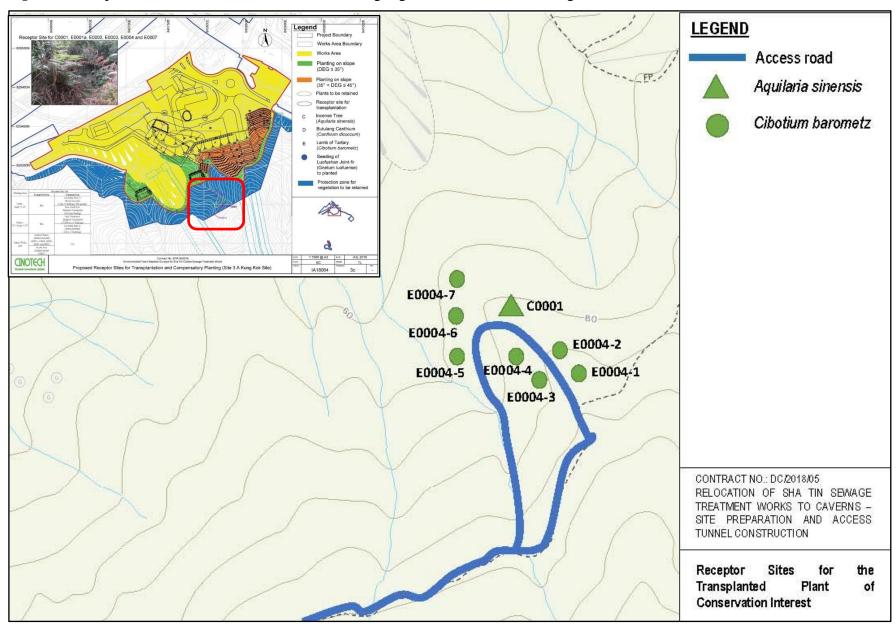

TABLE

Table 1. Recommendations on the recorded plant species of conservation importance (adopted from previously approved Protection and Transplantation Proposal Version 7.1).

					Re	ecommenda	tions	
Common Name	Species Name	Units	Retain	Transplant	Tag No.		Total	
Common Name	Species Name	Units				Fell	(in Project	Transplantation Date
							Boundary)	
Site 1								
						4800 (140		
				350 (228		confirmed		
				confirmed at		at Portion		
Small Persimmon	Diospyros vaccinioides	No.	950	Portion 12)	TBC	12)	6100	TBC
Luofushan Joint-fir	Gnetum luofuense	m2	300	0	NA	1700	2000	NA
Purple Bulb Orchid	Ania hongkongensis	No.	4	1	H0002	0	5	23/7/2019
Site 2								
Carall Daysins as an	Diocemunos massimisidos	Na	950	40	DV0001 DV0040	1500	2500	3/8/2019
Small Persimmon	Diospyros vaccinioides	No.	950	10	DV0001-DV0040	1500	2500	TBC
Luofushan Joint-fir	Gnetum luofuense	m2	300	0	NA	2500	2800	NA
Butulang Canthium	Canthium dicoccum	No.	1	0	NA	4	5	NA
Lamb of Tartary	Cibotium barometz	No.	0	19		2	21	TBC

Site 3											
Small Persimmon	Diospyros vaccinioides	No.	3700	100	TBC	7450	11100	TBC			
Luofushan Joint-fir	Gnetum luofuense	m2	750	0	NA	1900	2650	NA			
Butulang Canthium	Canthium dicoccum	No.	0	0	NA	4	4	NA			
					E0004-1 ~						
Lamb of Tartary	Cibotium barometz	No.	101	7	E0004-7	50	158	12/7/2019			
Incense Tree	Aquilaria sinensis	No.	0	1	C0001	0	1	12/7/2019			

Table 2. Conditions of the transplanted *Diospyros vaccinioides* at nursery in post-transplantation monitoring.

Date of			Health	Structural	Amenity	
monitoring	No.	Form	condition	condition	value	Remarks
	DV0001	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated
	DV0002	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated
	DV0003	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated
	DV0004	Fair	Fair	Fair	Fair	
	DV0005	Fair	Fair	Fair	Fair	Young leaves observed
	DV0006	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated
	DV0007	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated
	DV0008	Fair	Fair	Fair	Fair	Young leaves observed
	DV0009	Poor	Poor	Poor	Poor	Dead (certified on 12 Nov 2019)
	DV0010	Fair	Fair	Fair	Poor	No fresh foliage; dehydrated
	DV0011	Fair	Fair	Fair	Fair	Young leaves observed
	DV0012	Good	Good	Fair	Good	
	DV0013	Fair	Fair	Fair	Fair	
	DV0014	Fair	Fair	Fair	Fair	
	DV0015	Fair	Fair	Fair	Fair	Young leaves observed
	DV0016	Fair	Fair	Fair	Fair	Young leaves observed
	DV0017	Fair	Fair	Fair	Fair	Replaced
20-Feb-2020	DV0018	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated
	DV0019	Fair	Fair	Fair	Fair	Replaced
	DV0020	Fair	Fair	Fair	Fair	
	DV0021	Fair	Fair	Fair	Fair	
	DV0022	Fair	Fair	Fair	Fair	
	DV0023	Fair	Fair	Fair	Fair	Replaced
	DV0024	Fair	Fair	Fair	Poor	No fresh foliage; dehydrated
	DV0025	Fair	Fair	Fair	Fair	
	DV0026	Fair	Fair	Fair	Fair	
	DV0027	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated
	DV0028	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated
	DV0029	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated
	DV0030	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated
	DV0031	Poor	Poor	Poor	Poor	Dead (certified on 12 Nov 2019)
	DV0032	Poor	Poor	Poor	Fair	
	DV0033	Fair	Fair	Fair	Fair	Replaced
	DV0034	Fair	Fair	Fair	Fair	Young leaves observed
	DV0035	Fair	Fair	Fair	Fair	Young leaves observed
	DV0036	Poor	Poor	Poor	Poor	No fresh foliage; dehydrated

DV0037	Fair	Fair	Fair	Fair	
DV0038	Fair	Fair	Fair	Fair	Replaced
DV0039	Fair	Fair	Fair	Fair	
DV0040	Fair	Fair	Fair	Fair	

Note:

Height, spread and DBH is not applicable for undersized tree, shrubs and herbs.

Table 3. Conditions of the transplanted plants at receptor sites in post-transplantation monitoring.


Date of monitoring	No.	Form	Health condition	Structural condition	•	Remarks	
	C0001	Fair	Fair	Fair	Poor	Young leaves kept growing;	
						sign of yellow foliage	Quarterly
	E0004-1	Fair	Fair	Fair	Fair		monitoring
23 Dec 2019	E0004-2	Fair	Fair	Fair	Fair		(next
25 Dec 2019	E0004-3	Fair	Fair	Fair	Fair		monitoring
	E0004-4	Fair	Fair	Fair	Fair		will be scheduled in
	E0004-5	Fair	Fair	Fair	Fair		Mar 2020)
	E0004-6	Fair	Fair	Fair	Fair	Some leaves drop	10101 2020)
	E0004-7	Fair	Fair	Fair	Fair		
9 & 22 Jan 2020	H0002	Fair	Poor	Fair	Fair	Yellow leaf	Quarterly
						observed	monitoring
							(next
							monitoring
							will be
							scheduled in
							Apr 2020)


Note:

Height, spread and DBH is not applicable for undersized tree, shrubs and herbs.

APPENDIX 1

Photographic records of post-transplantation monitoring on plants of conservation importance transplanted at nursery

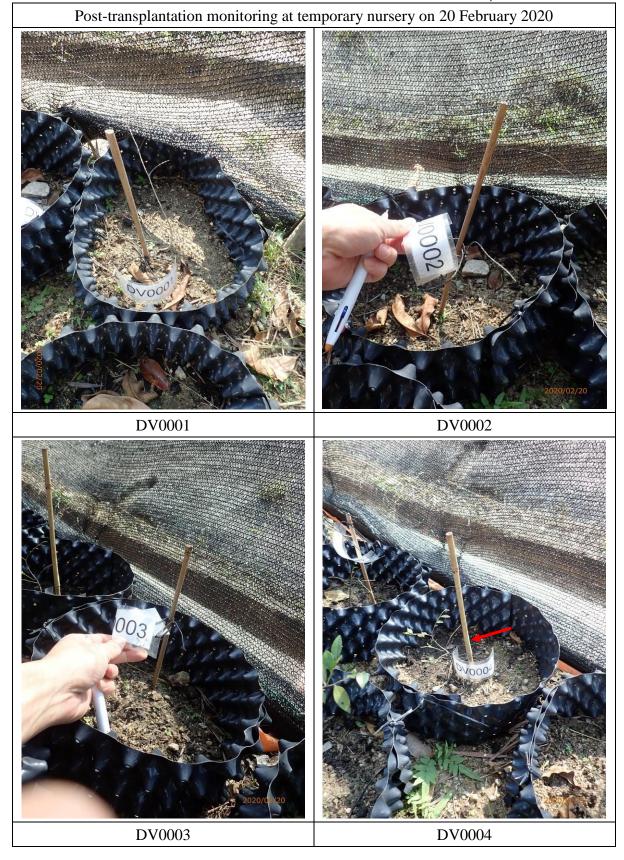


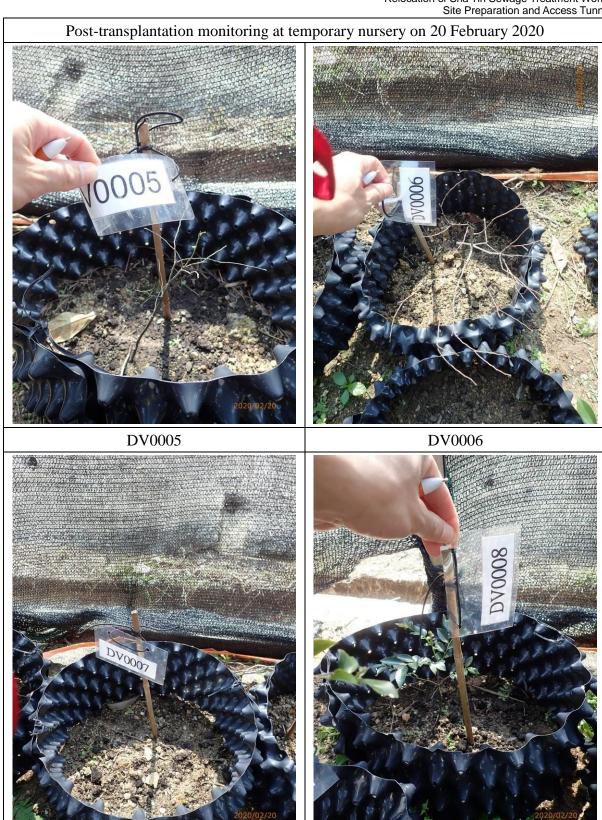


DV0008


DV0007




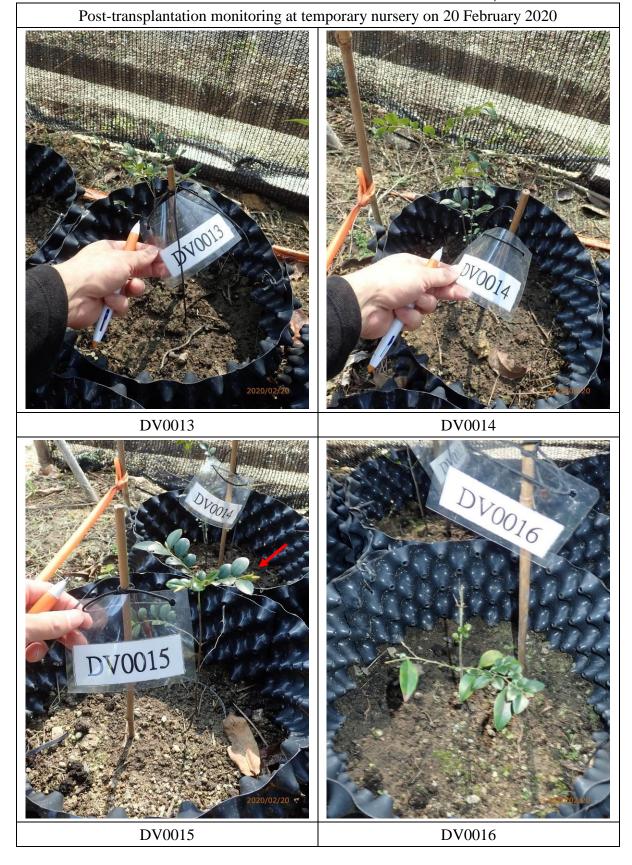

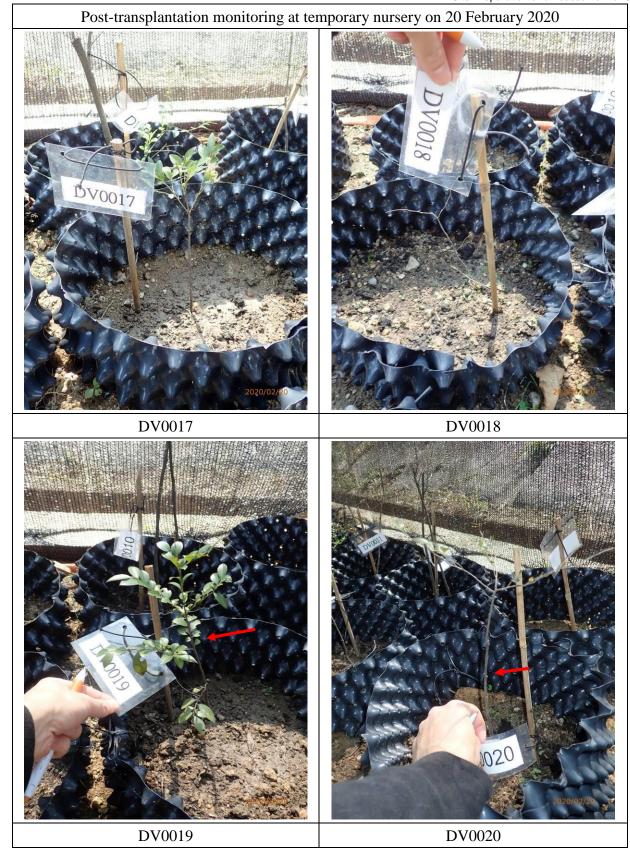




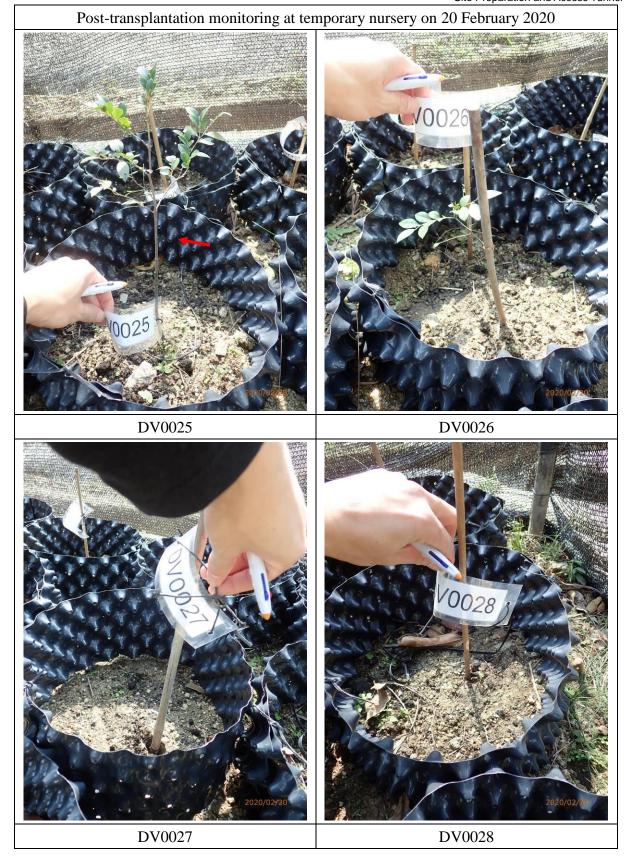

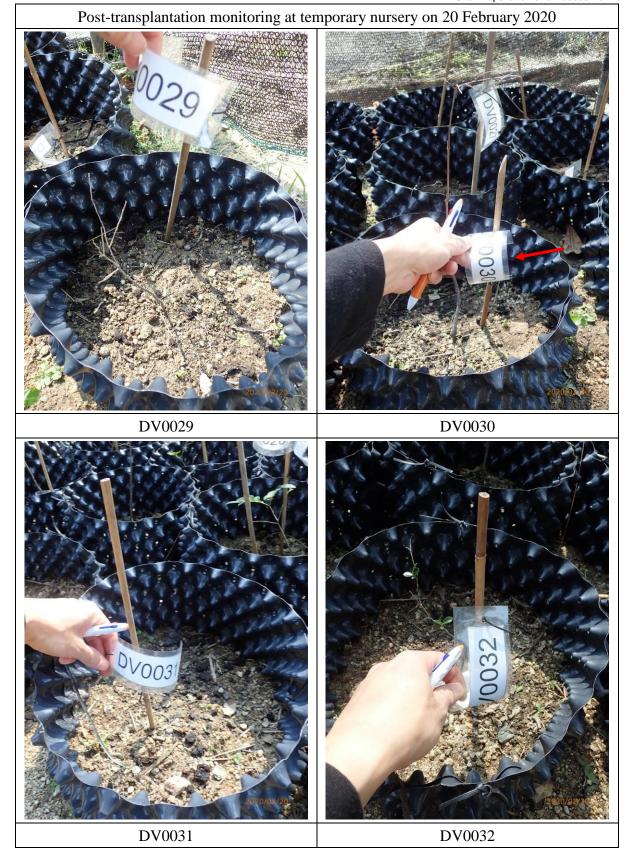




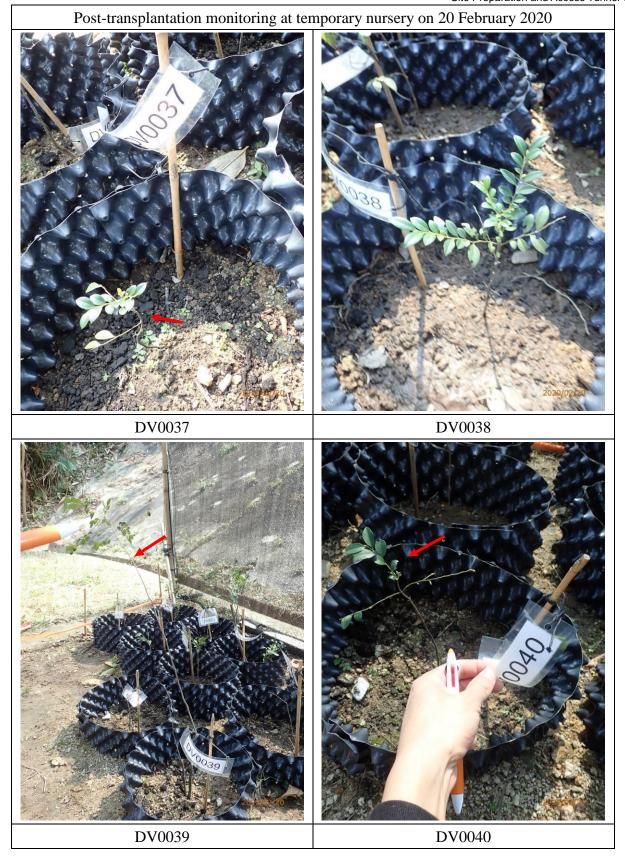

APPENDIX 2

Photographic records of post-transplantation monitoring on plants of conservation importance transplanted at receptor site

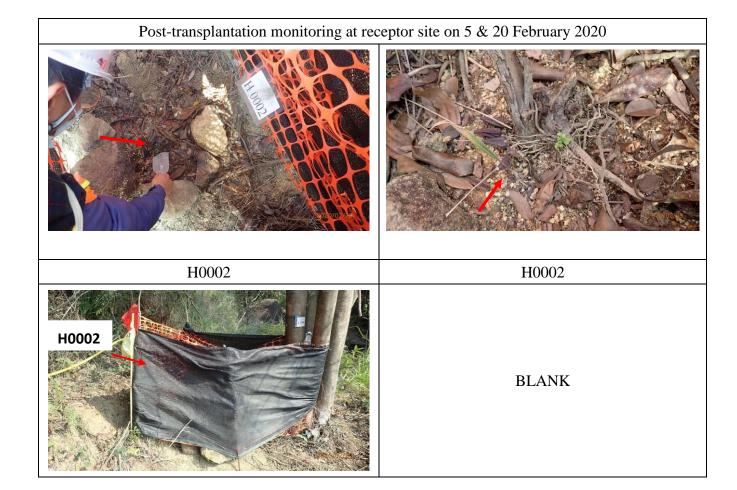

APPENDIX 3

Photographic records of bi-weekly ecological monitoring

On retained plants of conservation importance at Site 1



Appendix 3.1

Environmental Mitigation Implementation Schedule

APPENDIX C IMPLEMENTATION SCHEDULE OF RECOMMENDED MITIGATION MEASURES

C.1 Introduction

C.1.1 This section presents the implementation schedule of mitigation measures for the Project. **Table C.1** summarises the details of the recommended mitigation measures for all works areas. For each recommended mitigation measures, both the location and timing for the measure have clearly been identified as well as the parties responsible for implementing the measure and for maintenance (where applicable).

Table C.1 Implementation Schedule of Recommended Mitigation Measures

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion Sta	age ¹	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
	Air Qua	lity Impact							
	Construction Phase								
Table 3.5	2.4.1	The rock crushing plant is configured as an enclosed system. Dust collector with dust removal efficiency of 99% will be provided at the exhaust of the rock crusher during rock crushing. Watering will be provided to maintain material in wet condition. Vehicles would be required to pass through the wheel washing facilities provided at site exit.	Rock Crushing Plant / Construction Phase	Contractor	1	V		V	Air Pollution Control Ordinance (APCO)
3.8.1	2.4.1	Watering eight times a day on active works areas, exposed areas and unpaved haul roads to reduce dust emission by 87.5%.	All active works areas, exposed areas and unpaved haul roads	Contractor		1		√	APCO

¹ Des = Design; C = Construction; O = Operation; Dec = Decommissioning

Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion St	Relevant Legislation & Guidelines	
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
3.8.1	2.4.1	Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices:	Construction Sites	Contractor		1		1	APCO and Air Pollution Control (Construction Dust) Regulation
	•	Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather.	te ds, or on						
		Use of frequent watering for particularly dusty construction areas and areas close to ASRs.							
		Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.							
		 Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. 							
		 Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations. 							
		Establishment and use of vehicle wheel and body washing facilities at the exit points of the site.							
		 Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading area of barging point, and use of water sprinklers at the loading area 							

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	mentat	tion Sta	ige ¹	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods.							
		Provision of not less than 2.4m high hoarding from ground level along site boundary where adjoins a road, streets or other accessible to the public except for a site entrance or exit.							
		Imposition of speed controls for vehicles on site haul roads.							
		Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs.							
		Every stock of more than 20 bags of cement or dry PFA should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.							
		Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.							

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
	Operatio	n Phase							
3.5.2	-	Sludge tanks with totally enclosed design proven by DSD should be deployed for transporting sludge. With thorough cleaning practice and regular condition test of the sludge tanks, odour emission and leachate leakage during storage and transportation are not anticipated.	Cavern Sewage Treatment Works (CSTW) / Operation Phase	Project Proponent / Operator	√		√		-
3.6.2, 3.7.2	2.4.2	All treatment units with potential odour emission will be covered and the exhausted air will be conveyed to the deodouriser (with 80 – 97% odour removal efficiency) for treatment before discharge to the environment.	CSTW / Operation Phase	Design team / Project Proponent / Operator	√		√		-
3.7.2	2.4.2	The following appropriate odour control measures would be implemented. (i) Adopting the advantage of caverns as natural barriers for odour control; (ii) Covering up of odour sources; (iii) Preventing odour leakage through the access tunnels by applying negative pressure inside caverns; (iv) Installing deodourizing units to clean up the collected foul air; (v) Discharging exhausted air at height to further enhance the dilution effect; and (vi) Enhancing the odour management of the sludge transportation.	CSTW / Operation Phase	Design team / Project Proponent / Operator	1		\ \		-

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	ition St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
3.10.2	2.3.1	Odour monitoring at the inlet and outlet of the deodourizing units is proposed to be conducted for first three years of the operation of CSTW, quarterly in the first year, and once every 6 months in the second and third years if monitoring results remain below the limit levels.	CSTW / Operation Phase	Project Proponent / Operator	V		√		-
3.10.2	2.3.2	An Odour Complaint Registration System is also proposed in the EM&A programme to check whether the deodorizing units can fulfill the recommended odour removal performance.	CSTW / Operation Phase	Operator			V		-
3.10.2	-	Any unexpected leakage from tanks could be observed with monitoring equipment. Monitoring equipment would be installed in the CSTW to monitor the concentration of H ₂ S, CO and CO ₂ and methane. Investigation and repair works would be carried out immediately if abrupt increase of these concentrations are reported. Emergency Plan would be established for these upset conditions.	CSTW / Operation Phase	Project Proponent / Operator	1		V		-
	Noise In	npact							
	Construc	tion Phase							
4.5.1.6	-	Re-provision of 220m length noise barrier with 10mPD on temporary access haul road to replace the existing 150m length noise barrier with 9.2mPD to 10mPD on Ma On Sha Road. The	Proposed temporary access / Construction Phase	Contractor		√			Technical Memorandum on Environmental Impact Assessment Process (EIAO-TM), Noise Control Ordinance (NCO)

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		location of the relocated noise barrier is shown in Figure No. 60334056/EIA/4.02 and Appendix 4.07. Once the construction work for the CSTW is completed, the temporary access roads would be demolished and the relevant section of Ma On Shan Road and associated noise barrier would be recovered as before.							
4.8.1	3.8.1	The use of quiet plant associated with the construction works is prescribed in British Standard "Code of practice for noise and vibration control on construction and open sites, BS5228" which contains the SWLs for specific quiet PME.	All Construction Work Sites	Contractor		√		V	EIAO-TM, NCO
4.8.1	3.8.1	To alleviate the construction noise impact on the affected NSRs, movable noise barrier for Air Compressor, Bar Bender and Cutter, Breaker, Chisel, Saw, Compactor, Mixers, Pump, Crane, Desander, Drilling Rig, Dump Truck, Excavator, Generator, Grab, Lorry, Paver, Poker and Roller are proposed.	All Construction Work Sites	Contractor		√		√	EIAO-TM, NCO
4.8.1	3.8.1	Provision of noise barrier/acoustic mats for Drilling Jumbo so as to have screening effecting with 10 dB(A) noise attenuation	Drilling Jumbo operate outside the portal and within 20m inside the portal	Contractor		√			EIAO-TM, NCO
4.8.1	3.8.1	To further alleviate the construction noise impact on the Neighbourhood Advice-Action Council Harmony	Construction Site for access road for	Contractor		√		V	EIAO-TM, NCO

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	menta	tion St	age ¹	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		Manor, it is proposed to limit the number of on-time operating PMEs within 120m of this NSR during construction of access road.	magazine at A Kung Kok Road						
4.9.1	3.8.1	In addition to the above-mentioned mitigation measures, good site practices listed below shall be adopted by all the contractors to further ameliorate the noise impacts.	All Construction Work Sites	Contractor		√		1	EIAO-TM, NCO
		Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program.							
		Silencers or mufflers on construction equipment should be utilised and should be properly maintained during the construction program.							
		Mobile plant, if any, should be sited as far away from NSRs as possible.							
	•	Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum.							
		Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.							

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Implement Duration of Agent Measures /	Implementation Agent	Imple	menta	tion Sta	age ¹	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities.							
	Operatio	n Phase					<u> </u>		
4.7.4	3.8.2	The maximum allowable sound power levels for the ventilation shaft, ventilation buildings at main portal and emergency portal, ventilation fan for chiller plant room and cooling tower at the administration building as presented in Table 4.16 of the EIA Report should be achieved such that the nearest affected NSRs can be in compliance with the noise criteria	Ventilation Shaft, Administration Building and Ventilation Buildings/ Operation Phase	Project Proponent	√ 		√		EIAO-TM, NCO
4.11.2	3.8.2	Prior to the operational phase of the Project, a commissioning test for the ventilation buildings, the ventilation shaft, ventilation fan for chiller plant room at administration building and cooling tower at the administration building would be conducted to ensure compliance with the relevant allowable maximum sound power levels.	Ventilation Shaft, Administration Building and Ventilation Buildings/ Operation Phase	Contractor			√		EIAO-TM, NCO

EIA Ref.	EM&A Log			Implementation Agent	Implementation Stage ¹			tage 1	Relevant Legislation & Guidelines
	Ref.				Des	С	0	Dec	
	Water Q	uality Impact							
	Construc	ction Phase							
5.7.2	4.10	Water used in ground boring and drilling for site investigation or rock / soil anchoring should as far as practicable be re-circulated after sedimentation. When there is a need for final disposal, the wastewater should be discharged into storm drains via silt removal facilities.	Construction Sites / Construction Phase	Contractor		√			Water Pollution Control Ordinance (WPCO), EIAO-TM
5.7.2	4.10	All vehicles and plant should be cleaned before they leave a construction site to minimise the deposition of earth, mud, debris on roads. A wheel washing bay should be provided at every site exit if practicable and wash-water should have sand and silt settled out or removed before discharging into storm drains. The section of construction road between the wheel washing bay and the public road should be paved with backfill to reduce vehicle tracking of soil and to prevent site run-off from entering public road drains.	Construction Sites / Construction Phase	Contractor		V			Professional Persons Environmental Consultative Committee (ProPECC) Practice Note (PN) 1/94, WPCO, Waste Disposal Ordinance (WDO)
5.7.2	4.10	Good site practices should be adopted to remove rubbish and litter from construction sites so as to prevent the rubbish and litter from spreading from the site area. It is recommended to clean the construction sites on a regular basis.	Construction Sites / Construction Phase	Contractor		√			WPCO, EIAO-TM

EIA Ref.	EM&A Log	1	Location / Duration of	Implementation Agent	Implementation Stage ¹			age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
5.7.2	4.10	The site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" should be followed where applicable to minimise surface run-off and the chance of erosion.	Construction Sites / Construction Phase	Contractor		√			WPCO, EIAO-TM, ProPECC PN 1/94
5.7.2	4.10	There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the Technical Memorandum on Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters (TM-DSS). The beneficial uses of the treated effluent for other on-site activities such as dust suppression, wheel washing and general cleaning etc., can minimise water consumption and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the relevant WPCO licence which is under the ambit of RO of EPD.	Construction Sites / Construction Phase	Contractor		√			WPCO, EIAO-TM, (TM-DSS)
5.7.2	4.10	Contractor must register as a chemical waste producer if chemical wastes would be produced from the	Construction Sites / Construction Phase	Contractor		V			WPCO, EIAO-TM, WDO

EIA Ref.	EM&A Log		Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation, should be observed and complied with for control of chemical wastes.							
5.7.2	4.10	Any service shop and maintenance facilities should be located on hard standings within a bonded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	Construction Sites / Construction Phase	Contractor		√			WPCO, EIAO-TM
5.7.2	4.10	Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance should be followed to avoid leakage or spillage of chemicals.	Construction Sites / Construction Phase	Contractor		√ 			WPCO, EIAO-TM, WDO
5.7.2	4.10	Sufficient chemical toilets should be provided in the works areas. A licensed waste collector should be deployed to clean the chemical toilets on a regular basis.	Construction Sites / Construction Phase	Contractor		1			WPCO, EIAO-TM

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	ition St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
5.7.2	4.10	Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the surrounding environment.	Construction Sites / Construction Phase	Contractor		√			WPCO, EIAO-TM
5.7.2	4.10	The practices outlined in ETWB TC (Works) No. 5/2005 "Protection of natural streams/rivers from adverse impacts arising from construction works" should also be adopted where applicable to minimise the water quality impacts upon any natural streams or surface water systems.	Construction Sites / Construction Phase	Contractor		√			WPCO, EIAO-TM, ETWB TC (Works) No. 5/2005
5.7.2	4.10	Appropriate measures during the construction of the cavern construction should be implemented to minimise the groundwater infiltration.	Construction Sites / Construction Phase	Contractor		1			WPCO, EIAO-TM
5.7.2	4.10	No directly discharge of groundwater from contaminated areas should be adopted. Prior to any excavation works within the potentially contaminated areas at the existing STSTW site, the baseline groundwater quality in these areas should be reviewed based on the relevant SI data and any additional groundwater quality measurements to be performed with reference to Guidance Note for Contaminated Land Assessment and Remediation and the review results should be submitted to EPD for examination. If the review results indicated that the groundwater to be generated from the excavation	Construction Sites / Construction Phase	Contractor		V			WPCO, EIAO-TM, Guidance Note for Contaminated Land Assessment and Remediation

EIA Ref.	EM&A Log	.og	Location / Duration of	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		works would be contaminated, this contaminated groundwater should be either properly treated or properly recharged into the ground in compliance with the requirements of the TM-DSS. If wastewater treatment is to be deployed for treating the contaminated groundwater, the wastewater treatment unit shall deploy suitable treatment processes (e.g. oil interceptor / activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (such as TPH) to an undetectable range. All treated effluent from the wastewater treatment plant shall meet the requirements as stated in TM-DSS and should be either discharged into the foul sewers or tankered away for proper disposal.							
5.7.2	4.10	If deployment of wastewater treatment is not feasible for handling the contaminated groundwater, groundwater recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in section 2.3 of the TM-DSS. The baseline groundwater quality should be determined prior to the selection of the recharge wells, and submit a working plan to EPD for agreement. Pollution	Construction Sites / Construction Phase	Contractor		1			WPCO, EIAO-TM, TM- DSS

EIA Ref.	EM&A Log		Location / Duration of	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the recharge well. Groundwater monitoring wells should be installed near the recharge points to monitor the effectiveness of the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products should be removed as necessary by installing the petrol interceptor. The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater							
5.7.2	4.10	THEES connection works should be synchronized with the THEES maintenance, for a duration not longer than 4 weeks each outside the algae blooming season (January to May) and frequency of THEES maintenance shall be no more than once per year during the construction phase of the Project.	Tolo Harbour / Construction Phase	Project Proponent / Contractor	√	√			EIAO-TM
	Construc	ction and Operation Phases							
5.10.2	4.10	Shutdown of the THEES for maintenance should be shortened as far as possible. It is recommended that the maintenance of the THEES tunnel should be avoided during the algae blooming season (January to May).	Tolo Harbour / Construction and Operation Phase	Project Proponent		√	V		WPCO, EIAO-TM

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	ition St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
5.10.2	4.10	Relevant government departments including EPD, WSD, AFCD as well as the key stakeholders for mariculture and fisheries in Tolo Harbour should be informed of the maintenance event prior to any discharge.	Tolo Harbour / Construction and Operation Phase	Project Proponent		√	V		WPCO, EIAO-TM
5.10.3	4.2-4.5	An event and action plan and a water quality monitoring programme (as presented in the EM&A Manual) should be implemented for the THEES maintenance discharge	Tolo Harbour / Construction and Operation Phase	Project Proponent		V	√		WPCO, EIAO-TM
5.10.1	4.10	Silt screen may be installed at the flushing water intakes during the THEES maintenance discharge should it appear necessary. Close communication between DSD and WSD should be maintained to minimize any impact on the flushing water intakes due to THEES maintenance discharge.	WSD flushing water intakes / Construction and Operation Phase	WSD / Project Proponent		√	V		WPCO, EIAO-TM
	Design a	and Operation Phases							
5.8.3	4.6	In case adverse impact on KTN is identified based on the result of the three-month monitoring programme after commissioning of the project, the operation conditions of the treatment and THEES system should be investigated, and corrective and remedial action should be implemented to improve the effluent discharge from the CSTW. Furthermore, DSD should extend the water quality monitoring	Project site / Design and Operation Phases	Project Proponent			٨		WPCO, EIAO-TM

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		programme for at least three months or as agreed by the Director of Environmental Protection.							
5.11.2	4.10	Dual power supply or ring main supply from CLP Power Hong Kong Ltd. CLP should be provided for the CSTW to prevent the occurrence of power failure. In addition, standby facilities for the main treatment units and standby equipment parts / accessories should also be provided in order to minimise the chance of emergency discharge. CLP should be consulted in order to ascertain the power supply for normal plant operation within the caverns. It is recommended that government departments including EPD, WSD and AFCD as well as the key stakeholders for mariculture and fisheries in Tolo Harbour should be informed as soon as possible in case of any emergency discharge so that appropriate actions can be taken.	Project site / Design and Operation Phases	Project Proponent	1		V		WPCO, EIAO-TM
5.11.2	4.10	In case of emergency discharge, the plant operators of CSTW should carry out necessary follow-up actions according to the procedures of the current contingency plan formulated for the existing STSTW to minimise the water quality impact.	Project site / Operation Phase	Project Proponent			V		WPCO, EIAO-TM
5.11.2	4.10	WSD may also consider, should it appear necessary, to shut down the Sha Tin seawater pumping station for a short period of time in case of	Sha Tin seawater pumping station / Operation Phase	WSD / Project Proponent			V		WPCO, EIAO-TM

EIA Ref.	Ref. Log		Location / Duration of	Implementation Agent	Implementation Stage ¹			age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		emergency discharge in order to minimize any adverse impacts.							
5.13.2	4.10	Best Management Practices to reduce storm water and non-point source pollution are also proposed as follows:	Project site / Design and Operation Phase	Project Proponent	√		√		WPCO, ProPECC PN 5/93
	Design Measures								
		Exposed surface shall be avoided within the road and portal sites to minimise soil erosion. The access road and the portal areas shall be either hard paved or covered by landscaping area where appropriate.							
		Streams near the Project site will be retained to maintain the original flow path. The drainage system will be designed to avoid flooding.							
		Green areas / planting etc. should be introduced alongside the access road and within the portal areas, as far as possible, to minimise runoff pollution.							
		Devices/ Facilities to Control Pollution							
		 Screening facilities such as standard gully grating and trash grille, with spacing which is capable of screening off large substances such as fallen leaves and rubbish should be provided at the inlet of drainage system. 							
		Road gullies with standard design and silt traps should be provided to							

EIA Ref.	EM&A Log	Dura	Location / Duration of	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		remove particles present in stormwater runoff, where appropriate.							
		Administrative Measures							
		Good management measures such as regular cleaning and sweeping of road surface/ open areas are suggested. The road surface/ open area cleaning should also be carried out prior to occurrence rainstorm.							
		Manholes, as well as stormwater gullies, ditches provided at the Project site should be regularly inspected and cleaned (e.g. monthly). Additional inspection and cleansing should be carried out before forecast heavy rainfall.							
	Land Co	ntamination							
6.7.1	-	Further site walkover and/or detailed land contamination assessment will be required for sites that are inaccessible or currently in operation / yet to be constructed (i.e. existing STSTW, David Camp and part of existing Sha Tin VDC, and proposed A Kung Kok Shan Road surface magazine site within the Project boundary). The site walkover, detailed land contamination assessment and if necessary, remediation works should be carried out after decommissioning of the sites	Existing STSTW, David Camp and VDC / Construction Phase	Project Proponent / Contractor		V		√ (for exist ing STS TW)	Guidance Note for Contaminated Land Assessment and Remediation, Practice Guide for Investigation and Remediation of Contaminated Land, Guidance Manual for Use of Risk-based Remediation Goals for Contaminated Land Management

EIA Ref.	Ref. Log		Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		but prior to re-development and should include the following:							
		Prior to the commencement of the SI works, review the CAP to confirm whether the proposed SI works (e.g. sampling locations, testing parameters etc.) are still valid and to confirm the appropriate RBRGs land use scenario for the development;							
		Submit supplementary CAP(s), presenting the findings of the above review for EPD endorsement. If land contamination issues were identified within David Camp or part of existing VDC / proposed A Kung Kok Shan Road surface magazine site within the Project boundary in the further site walkover, findings of the site walkover and the proposal for SI works should also be presented in the supplementary CAP(s);							
		 Carry out SI works according to the supplementary CAP endorsed by EPD; 							
		Submit CAR(s), detailing findings of the SI works and nature/extent of any soil/groundwater contamination, and, if contaminated identified, RAP(s), discussing the appropriate remedial methods and mitigation							

EIA Ref.	EM&A Log	1	Location / Duration of	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		measures, for the identified contamination, for EPD agreement; and							
		Carry out soil/groundwater remediation works according to EPD agreed RAP and submit RR(s) afterwards for EPD agreement. The remediation works and agreement of RR should be completed prior to redevelopment.							
6.7.2		If contamination were identified, mitigation measures as recommended in the RAP should be followed and should include the following: • Excavation profiles must be properly designed and executed with attention to the relevant requirements for environment, health and safety; • Excavation shall be carried out during dry season as far as possible to minimise contaminated runoff from contaminated soils; • Supply of suitable clean backfill material (or treated soil) after excavation; • Stockpiling site(s) shall be lined	Project Site / Construction Phase	Contractor		√ ·		√ (for exist ing STS TW)	Guidance Note for Contaminated Land Assessment and Remediation, Practice Guide for Investigation and Remediation of Contaminated Land, Guidance Manual for Use of Risk-based Remediation Goals for Contaminated Land Management
		Stockpiling site(s) shall be lined with impermeable sheeting and bunded. Stockpiles shall be fully covered by impermeable sheeting to reduce dust emission. If this is not practicable due to frequent							

EIA Ref.	EM&A Log	Environmental Protection Measures	Duration of Agent	on Implementation Stag		age ¹	Relevant Legislation & Guidelines		
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		usage, regular watering shall be applied. However, watering shall be avoided on stockpiles of contaminated soil to minimise contaminated runoff.							
		Vehicles containing any excavated materials shall be suitably covered to limit potential dust emissions or contaminated wastewater run-off, and truck bodies and tailgates shall be sealed to prevent any discharge during transport or during wet conditions;							
		Speed control for the trucks carrying contaminated materials shall be enforced;							
		Vehicle wheel and body washing facilities at the site's exist points shall be established and used; and							
		Pollution control measures for air emissions (e.g. from biopile blower and handling of cement), noise emissions (e.g. from blower or earthmoving equipment), and water discharges (e.g. runoff control from treatment facility) shall be implemented and complied with relevant regulations and guidelines.							

EIA Ref.	EM&A Log	,	Location / Duration of	Agent	Implementation Stage ¹				Relevant Legislation & Guidelines		
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec			
	Hazard to Life										
	Constru	ction Phase									
7.14.1	6.2.2	The following recommendations are justified to be implemented to meet the EIAO-TM requirements: The truck should be designed to minimise the amount of combustible in the cabin. The fuel carried in the fuel tank should also be minimised to reduce the duration of any fire; The accident involvement frequency of the explosives delivery truck should be minimised through implementation of several administrative measures, such as providing training programme to the driver, regular "tool box" briefing session, implementing a defensive driving attitude, selecting driver with good safety record, and providing regular medical checks for the driver; Avoidance of returning unused explosives to the magazine, only the required quantity of explosives for a particular blast should be transported; Maintain a minimum headway of 10 minutes between two	Explosives dlivery route / Construction Phase	Contractor	1	V			EIAO-TM		

EIA Ref.	EM&A Log		Location / Duration of	Implementation Agent	Imple	ementa	tion Sta	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		consecutive truck convoys whenever practicable; and							
		The fire involvement frequency should be minimised by carrying better types of fire extinguishers and with bigger capacity onboard of the explosives delivery truck. Emergency plans and trainings could also be provided to make sure that the fire extinguishers are used adequately.							
7.14.2	6.2.3	The magazine should be designed, built, operated and maintained in accordance with Mines Division's guidelines and appropriate industry best practice. In addition, the following recommendations should be implemented:	Magazine Site/ Construction Phase	Contractor	V	√			-
		The security plan should address different alert security level to reduce opportunity for arson or deliberate initiation of explosives;							
		Emergency plan should be developed to address uncontrolled fire in magazine area, and drill of the emergency plan should be regularly carried out;							
		Suitable work control system should be set-up, such as an operational manual including Permit-to-Work system, to ensure that work activities undertaken							

EIA Ref.	EM&A Log		Location / Duration of	Implementation Agent	Imple	ementa	tion Sta	age ¹	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		during operation of the magazine are properly controlled;							
		 Good house-keeping within the magazine to ensure no combustible materials are accumulated; 							
		 Good house-keeping outside the magazine stores to ensure no combustible materials are accumulated; and 							
		 Regular checking of the magazine store to ensure no water seepage through the roof, walls or floor. 							
7.14.3	6.2.4	The following recommendations should be implemented: • Emergency plan should be developed to address uncontrolled fire during transport. Case of fire near an explosive delivery truck in jammed traffic should be included in the plan. Activation of fuel and battery isolation switches on vehicle when fire breaks out should also be included in the emergency plan to reduce likelihood of prolonged fire leading to explosion; • Working guideline should be developed to define procedure for explosives transport during adverse weather such as thunderstorm;	To and from Magazine Site / Construction Phase	Contractor	√	√			-

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	tion of Agent		Implementation Stage		Relevant Legislation & Guidelines	
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		Detonators should be transported separately from other Class 1 explosives. Separation of vehicles should also be maintained through the trip;							
		Develop procedure to ensure the availability of parking space on site for the explosives delivery truck. Delivery should not be commenced if parking space on site is not secured;							
		 Hot work or other activities should be banned in the vicinity of the explosives offloading or charging activities; 							
		Lining should be provided within the transportation box on the vehicle;							
		Fire screen should be used between cabin and the load on the vehicle;							
		Ensure packaging of detonators remains intact until handed over at blasting site;							
		Ensure that cartridged emulsion packages are not damaged before every trip; and							
		Use experienced driver with good safety record.							

EIA Ref.	EM&A Log	Di	Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
7.14.4	6.2.5	The following recommendations should be implemented for the safe use of explosives:	CSTW / Construction Phase	Contractor	√	1			-
		Blast Charge Weight should be within MIC as specified for the given blast face;							
		Temporary mitigation measures such as blast doors or heavy duty blast curtains should be installed at the portals or shafts and at suitable locations underground to prevent flyrock and control the air overpressure;							
		Multiple faces blasting will be carried out for the construction of cavern in this project. Good communication and control will need to be adopted in ensuring that the works are carried out safely;							
		It is not intended to carry out complete evacuation of the construction areas and secure refuge areas should be identified to workers in the areas;							
		A Chief Shotfirer and a Blasting Engineer shall be employed in addition to the normal blasting personnel to ensure that the works are safe and coordinated between blasting areas;							
		Shotfirer to be provided with a lightning detector, and appropriate							

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent			age 1	Relevant Legislation & Guidelines	
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		control measures should be in place;							
		Speed limit for the diesel vehicle truck and bulk emulsion truck in the access tunnel and cavern should be imposed. The truck may be escorted while underground to ensure route is clear from hazards and obstructions; and							
		Hot work should be suspended during passage of the diesel vehicle truck and bulk emulsion truck in the access tunnel and cavern.							
		A boulder survey should be undertaken based on the likely PPV values that would result from the blasting process. Those boulders subject to the vibration higher than the allowable limit should be strengthened, removed, or constructed with boulder fence, prior to the commencement of blasting.							
	Operation	n Phase							
		Nil							

EIA Ref.	EM&A Log		Location / Duration of	Implementation Agent	Implement		nentation Stage ¹		Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
	Ecologic	cal Impact (Terrestrial and Marine)							
	Construc	tion Phase							
8.8.2	7.2.1	Construction of access roads and other temporary works should be carefully designed (e.g. elevated road for crossing streams) to avoid / minimise habitat loss and fragmentation.	Project site – areas access road / Pre-Construction Phase	Design team / Project Proponent	√				-
8.8.3	7.2.2	Minimise habitat loss to nearby habitats and associated wildlife by implementing the following mitigation measures: - • confining the works within the site boundary; • controlling access of site staff to avoid damage to the vegetation in surrounding areas; and • placement of equipment or stockpile in the existing disturbed / urbanised land within the site boundary of the Project to minimise disturbance to vegetated areas;	Project site / Construction Phase	Contractor		1			-
8.8.3	7.2.2	Reinstatement planting should be implemented upon the completion of construction works to minimise the ecological impact arising from the temporary habitat loss	Project Site (Main Portal Area / Secondary Portal Area / Access Road / Temporary Works Area) /Construction Phase	Project Proponent	√	√		√	

EIA Ref.	EM&A Log		Location / Duration of	Implementation Agent	Implementation Stage ¹			age ¹	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
8.8.2, 8.8.3 & 8.10	7.2.2	Detailed Vegetation Survey shall be conducted by a suitably qualified botanist / ecologist within the works area requiring vegetation clearance prior to commencement of works to identify plant species of conservation importance. The potentially affected individuals	Proposed works areas (Main Portal, Secondary Portal, Access Road) / Pre-Construction Phase	Project Proponent / Qualified botanist or ecologist		V			
		shall be tagged and fenced off for preservation, and in the case of unavoidable loss, for transplantation to nearby suitable habitat(s).							
8.8.2, 8.8.3 & 8.10	7.3.1	A Protection and Transplantation Proposal including the subsequent monitoring visit for the affected plant species should be prepared and conducted by a suitably qualified local ecologist. The Proposal should be submitted for approval at least one month before works commencement.	Recipient Site for transplanted species / Construction Phase	Project Proponent / Qualified botanist or ecologist		1			
		To review the performance of the transplantation exercise, monitoring of transplanted flora should be conducted monthly after the transplantation throughout the construction phase. The parameters to be monitored should include the health condition and survival rate of the transplanted flora and presence of weedy species. Any observations and recommendations should be reported in monthly EM&A reports							

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
8.8.3	7.2.2	Mitigation measures should be implemented to control runoff from the construction site, as well as the adopting guidelines and good site practices for handling and disposal of construction discharges in order to minimise the potential indirect impact on the streams (particularly S2) resulting from site runoff.	Access Road on Nui Po Shan / Construction Phase	Contractor		1			ETWB TCW No. 5/2005
		Precautionary measures should also be implemented to minimise indirect impacts to the streams, such as isolating the work site by placing sandbags and silt curtains, covering up construction materials, debris and spoil to avoid being washed into the stream, and properly collecting and treating construction effluent and sewage.							
8.8.3	7.2.2	Implement good site practice to further minimise impacts from disturbance such as noise, air quality and water quality issues, such as: -	Project site / Construction Phase	Contractor		√			-
		 the use of quiet plant and EPD's QPME and the availability of British Standards 5228 has been considered; 							
		 the use of movable noise barrier; the use of temporary noise screening structures or purpose- built temporary noise barriers; 							

EIA Ref.	EM&A Log		Location / Duration of	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		 install site hoarding as temporary noise barrier where construction works are undertaken; 							
		only well-maintained plant should be operated on site and plant should be serviced regularly during the construction programme;							
		Mitigation measures stipulated in the ProPECC PN 1/94 "Construction Site Drainage" should be complied to minimise water quality impact;							
		Installation of stand-by pump, emergency power supply and telemetry system to avoid sewage overflow and surcharge to sewerage system due to power/equipment failure.							
8.8.3	7.2.2	Minimise groundwater infiltration during cavern construction with the following water control strategies:-	Project site / Construction Phase	Contractor		√			-
		Probing Ahead: As a normal practice, the Contractor will undertake rigorous probing of the ground ahead of excavation works to identify zones of significant water inflow. The probe drilling results will be evaluated to determine specific grouting requirements in line with the tunnel / cavern advance. In such zones of significant water inflow that could occur as a result of discrete, permeable features, the intent							

EIA Ref.	EM&A Log		Duration of	Implementation Agent	Implementation Stage ¹			age ¹	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		would be to reduce overall inflow by means of cut-off grouting executed ahead of the tunnel / cavern advance;							
		Pre-grouting: Where water inflow quantities are excessive, pre- grouting will be required to reduce the water inflow into the tunnel / cavern. The pre-grouting will be achieved via a systematic and carefully specified protocol of grouting;							
		In principle, the grout pre-treatment would be designed on the basis of probe hole drilling ahead of the tunnel / cavern face;							
		The installation of waterproof lining would also be adopted after the formation of the tunnels and caverns.							
8.8.3	7.2.2	In the event of excessive infiltration being observed as a result of the tunnelling or excavation works even after incorporation of the water control strategies, post-grouting should be applied as far as practicable as described below:	Project site / Construction Phase	Contractor		√			-
		Post-grouting: Groundwater drawdown will be most likely due to inflows of water into the tunnel / cavern that have not been sufficiently controlled by the pregrouting measures in high permeability area. Where this							

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	tation Implementation Stage		age ¹	Relevant Legislation & Guidelines	
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		occurs post grouting will be undertaken before the lining is installed. Whilst unlikely to be required in significant measure, such a contingency should be allowed for reduction in permeability of the tunnel / cavern surround (by grouting) to limit inflow to acceptable levels.							
		The practical groundwater control measures stated above are proven technologies and have been extensively applied in other past projects. These measures or other similar methods, as approved by the Engineer to suit the works condition shall be applied to minimise the groundwater infiltration.							
8.8.3	7.2.2	In case seepage of groundwater occurs, groundwater should be pumped out from works areas and discharged to the storm system via silt trap. Uncontaminated groundwater from dewatering process should also be discharged to the storm system via silt removal facilities.	Project site / Construction Phase	Contractor		√			-

EIA Ref.	EM&A Log	g	Duration of	Implementation Agent				Relevant Legislation & Guidelines	
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
8.8.3	7.2.2	Mitigation measures recommended in the water quality impact assessment for controlling water quality impact will also serve to protect marine ecological resources from indirect impacts and ensure no unacceptable impact on marine ecological resources.	Tolo Harbour / Construction Phase	Contractor and Operator		√			-
		Relevant government departments including EPD, WSD and AFCD as well as key stakeholders for mariculture and fisheries in Tolo Harbour should be informed of the THEES maintenance / emergency discharge event prior to any discharge.							
		It is recommended that the temporary effluent bypass event and the THEES maintenance period should be shortened as far as possible.							
	Construc	tion and Operation Phase							
8.8.3	7.2.2	Overall reduction of glare during both construction and operation phase should be considered. A balance between lighting for safety, and avoiding excessive lighting can be achieved through the use of directional lighting to avoid light spill into sensitive areas, and control/timing of lighting periods of some facilities, particularly at the secondary portal which lies approximately 200 m northwest of Ma On Shan Country Park.	Project site / Construction and Operation Phase	Contractor and Operator		٧	√		-

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
8.8.3	7.2.2	During the decommissioning and demolition of the existing STSTW, the direction and lighting periods should be controlled during ardeid breeding season (March to August) to minimise the potential indirect impact on Penfold Park Egretry and the ardeids flying over the existing STSTW.	Existing STSTW / Decommissioning / March to August	Contractor				√	-
8.10	7.3	It is anticipated that the construction of rock caverns would not have adverse impacts on groundwater in Nui Po Shan. Nonetheless, surface water level or groundwater level near the caverns will be closely monitored during the construction and operation stage.	Project site / Construction and Operation Phase	Contractor and Operator		√	V		-
	Compens	satory Planting		I	I				
8.8.4& 8.10.1	7.2.3	Compensatory planting would be provided at main and secondary portal areas, and along the access road.	Main portal, secondary portal, and along access road	Project Proponent	√	√			DEVB TC(W) No. 7/2015
8.8.4 & 8.10.1	7.2.3	To facilitate successful planting, a detailed Woodland Compensation Plan should be prepared by local ecologists with at least 10 years relevant experience to form the basis of the proposed compensatory planting. The Woodland Compensation Plan should include implementation details, management requirement, as well as monitoring requirements (e.g. frequency and parameters) of the	Compensatory planting area (Main portal, secondary portal, and along access road) / pre- construction	Project Proponent	V	٧			

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		compensatory planting area. Approval of the Plan should be obtained from EPD at least three months before the prior to commencement of compensatory woodland planting.							
8.8.4 & 8.10.1	7.2.3	Upon the completion of planting, monitoring of the woodland compensation areas should be implemented, with maintenance works (e.g. irrigation, weeding, pruning, control of pests and diseases, replacement planting, repair of damage, etc.) conducted as necessary.	Compensatory planting area (Main portal, secondary portal, and along access road) / Operation	Project Proponent / CSTW Operator			√		
	Fisherie	s Impact							
9.6	8.2	Potential impacts on fisheries resources and fishing operations arising from the Project have been avoided and minimised by construction of a connection pipes to the existing emergency outfall of STSTW by trenchless method underneath Shing Mun River with the least water quality impact. In addition, the temporary effluent bypass event for THEES connection work would be synchronized within regular THEES maintenance. Therefore, additional water quality impact and fisheries impact from changes of water quality have been avoided. Furthermore, the THEES maintenance discharge would avoid the blooming season of algae (i.e. January to May) to minimise the potential water quality impacts. It is	Tolo Harbour /Construction and Operation Phase	Project Proponent / Contractor	√	√			-

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		recommended that any THEES maintenance period should be shortened as far as possible.							
9.6	8.2	Mitigation measures recommended in the water quality impact assessment for controlling water quality impact will also serve to protect fisheries from indirect impacts and ensure no unacceptable impact on fisheries resources and operations. For more detailed mitigation measures regarding water quality refer to Sections 5.7.2 and 5.13.2 of the EIA Report.	Construction and Operation Phase	Contractor and Operator		1	√		-
9.6	8.2	Relevant government departments including EPD, WSD and AFCD as well as key stakeholders for mariculture and fisheries in Tolo Harbour should be informed prior to the THEES maintenance / emergency discharge events.	Tolo Harbour / Construction and Operation Phase	Project Proponent		√	V		
	Landsca	pe and Visual Impact							
Table 10.10	-	CM1 - Preservation of Existing Vegetation	Construction Sites/ Construction Phase	Project Proponent	1	1		√	DEVB TCW No. 7/2015 and latest Guidelines on Tree Preservation during Development issued by GLTM Section of DEVB
Table 10.10	-	CM2 - Transplanting of Affected Trees	Construction Sites/ Construction Phase	Project Proponent	1	1		V	DEVB TCW No. 7/2015 and the latest Guidelines on Tree Transplanting issued by GLTM Section of DEVB

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
Table 10.10	-	CM3 - Compensatory Tree Planting	Construction Sites/ Construction Phase	Project Proponent	√	√		√	DEVB TCW No. 7/2015
Table 10.10	-	CM4 - Control of Night-time Lighting Glare	Construction Sites/ Construction Phase	Project Proponent	√	1		√	
Table 10.10	-	CM5 - Erection of Decorative Screen Hoarding	Construction Sites/ Construction Phase	Project Proponent	√	1		√	
Table 10.10	-	CM6 - Management of Construction Activities and Facilities	Construction Sites/ Construction Phase	Project Proponent	√	1		√	
Table 10.10	-	CM7 - Reinstatement of Temporarily Disturbed Landscape Areas	Construction Sites/ Construction Phase	Project Proponent	√	1		√	
Table 10.11	-	OM1 - Tree and Shrub Planting at the Temporary Project Magazine Site after Completion of Engineering Works	Temporary Project Magazine Site / Operation Phase	Project Proponent	√	1	1		
Table 10.11	-	OM2 - Aesthetically pleasing design of Aboveground Structures	Tunnel Portals, Administration Building, Ventilation Buildings, Electrical Substations and Ventilation Shaft / Operation Phase	Project Proponent	√	√	V		

EIA Ref.	EM&A Log		Location / Duration of	Implementation Agent	Imple	ementa	tion S	tage 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
Table 10.11	-	OM3 - Aesthetically pleasing design of Highways Structures	Access Road to Ventilation Shaft / Operation Phase	Highways Department	√	1	1		
Table 10.11	-	OM4 - Reprovision of Cycle Track	Cycle track / Operation Phase	Highways Department	V	V	1		
Table 10.11	-	OM5 - Provision of Green Roof	Administration Building and Ventilation Buildings / Operation Phase	Project Proponent	V	V	√		
Table 10.11	-	OM6 - Provision of Buffer Planting	Main and Secondary Portal Areas / Operation Phase	Project Proponent	1	√	√		
Table 10.11	-	OM7 - Hydroseeding on the disturbed ground surface after demolition works prior to future redevelopment of the existing STSTW	Existing STSTW / Operation Phase	Lands Department (LandsD) or future development agent in existing STSTW	√	√	٧		
Table 10.11	-	OM8 - Woodland Mix Planting on Soil Slopes	Soil Slopes / Operation Phase	Project Proponent	V	√	V		

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
	Cultural	Heritage Impact							
11.5.1.1	10.1.1	No potential direct or indirect impact to cultural heritage resource is anticipated, and therefore no mitigation measures are required.	N/A	N/A					EIAO EIAO-TM Antiquities and Monuments Ordinance Guidelines for Cultural Heritage Impact Assessment
	Wastes	Management Implications				•	•	•	
12.6.2	11.2.2	Appropriate waste handling, transportation and disposal methods for all waste arising generated during the construction works for the Project should be implemented to ensure that construction wastes do not enter the nearby streams or drainage channel. It is anticipated that adverse impacts would not arise on the construction site, provided that good site practices are strictly followed. Recommendations for good site practices during the construction activities include: Nomination of approved personnel, such as a site manager, to be responsible for good site practices, and making arrangements for collection of all wastes generated at the site and effective disposal to an appropriate facility.	Project Site Area / Construction Phase	Contractor		V		V	Waste Disposal Ordinance

EIA Ref.	Ref. Log		Location / Duration of	Implementation Agent	Imple	ementa	tion St	Relevant Legislation & Guidelines	
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		Training of site personnel in proper waste management and chemical waste handling procedures.							
		 Provision of sufficient waste reception/ disposal points, of a suitable vermin-proof design that minimises windblown litter. 							
		 Arrangement for regular collection of waste for transport off-site and final disposal. 							
		 Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers. 							
		 Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. 							
		 A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be proposed. 							
		A Waste Management Plan should be prepared and should be submitted to the Engineer for approval. One may make reference to ETWB TCW No. 19/2005 for details.							
		In order to monitor the disposal of C&D material at landfills and public filling areas, as appropriate, and to control fly tipping, a trip-ticket system should be included as one of the contractual							

EIA Ref.	EM&A Log		Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		requirements to be implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. One may make reference to DEVB TCW No.6/2010 for details.							
12.6.3	11.2.3	Good management and control of construction site activities / processes can minimise the generation of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:	Project Site Area / Construction Phase	Contractor		V		√	Waste Disposal Ordinance
		Segregate and store different types of construction related waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.							
		Provide separate labelled bins to segregate recyclable waste such as aluminium cans from other general refuse generated by the work force, and to encourage collection by individual collectors.							
		Any unused chemicals or those with remaining functional capacity shall be recycled.							
		Maximising the use of reusable steel formwork to reduce the amount of C&D material.							
		Prior to disposal of C&D waste, it is recommended that wood, steel							

EIA Ref.	EM&A Log		Location / Duration of	Implementation Agent	Implementation Stage ¹				Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill.							
		On-site crushing and sorting facilities are being considered to reduce the rock size to fulfill the size requirements from relevant waste collection / transfer / disposal facilities;							
		 Adopt proper storage and site practices to minimise the potential for damage to, or contamination of, construction materials. 							
		 Plan the delivery and stock of construction materials carefully to minimise the amount of surplus waste generated. 							
		Adopt pre-cast construction method instead of cast-in-situ method for construction of concrete structures as much as possible; and							
		Minimise over ordering of concrete, mortars and cement grout by doing careful check before ordering.							
		In addition to the above measures, other specific mitigation measures are recommended below to minimise environmental impacts during handling, transportation and disposal of wastes.							

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
12.6.4	11.2.4	Storage of materials on site may induce adverse environmental impacts if not properly managed, recommendations to minimise the impacts include:	Project Site Area / Construction Phase	Contractor		√		1	-
		Waste, such as soil, should be handled and stored well to ensure secure containment, thus minimising the potential of pollution;							
		Maintain and clean storage areas routinely;							
		Stockpiling area should be provided with covers as much as practicable and water spraying system to prevent materials from wind-blown or being washed away; and							
		Different locations should be designated to stockpile each material to enhance reuse.							
12.6.4	11.2.4	Licensed waste haulers should be employed for the collection and transportation of waste generated. The following measures should be enforced	Project Site Area / Construction Phase	Contractor		V		√	Waste Disposal Ordinance
		to minimise the potential adverse impacts:							Waste Disposal (Charges for Disposal of
		Remove waste in timely manner;							Construction Waste) Regulation
		Waste collectors should only collect wastes prescribed by their permits;							Land (Miscellaneous
		Impacts during transportation, such as dust and odour, should be							Provisions) Ordinance

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion Sta	age ¹	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		mitigated by the use of covered trucks or in enclosed containers;							
		Obtain relevant waste disposal permits from the appropriate authorities, in accordance with the Waste Disposal Ordinance (Cap. 354), Waste Disposal (Charges for Disposal of Construction Waste) Regulation (Cap. 345) and the Land (Miscellaneous Provisions) Ordinance (Cap. 28); Waste should be disposed of at							
		licensed waste disposal facilities; and Maintain records of quantities of							
		waste generated, recycled and disposed.							
12.6.4	11.2.4	Land transport will be used for transportation of excavated and stockpile materials. It is expected there will be 1260 vehicles per day for transporting waste during peak construction phase. The tentative transportation routings for the disposal of various types of wastes are shown in Table 12.4. The transportation routing may be changed subject to the traffic conditions. Nevertheless, it is anticipated that there is no adverse impact from the waste during transportation with the implementation of appropriated measures (e.g. using water-tight containers and covered trucks).	Transportation Route of Waste / Construction Phase	Contractor		1			-

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	ition St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
12.6.4	11.2.4	In order to monitor the disposal of C&D materials at PFRFs and landfills and to control fly-tipping, a trip-ticket system should be established in accordance with DEVB TCW No. 6/2010. A recording system for the amount of waste generated, recycled and disposed, including the disposal sites, should also be set up. Warning signs should be put up to remind the designated disposal sites. Close-circuited television should be installed at the vehicular entrance and exit of the site as additional measures to prevent fly-tipping.	Project Site Area / Construction Phase	Contractor		√ ·		~	DEVB TCW No. 6/2010
12.6.4	11.2.5	In addition to the above general measures, other specific mitigation measures on handling the C&D materials and materials generated from site formation and demolition work are recommended below, which should form the basis of the WMP to be prepared by the contractor(s) in construction phase.	Project Site Area / Construction Phase	Contractor		√		√	Technical Circular (Works) No. 19/2005 Environmental Management on Construction Site
12.6.5	11.2.5	In order to minimise the impact resulting from collection and transportation of C&D materials for off-site disposal, the excavated material arising from site formation and foundation works should be reused on-site as backfilling material and for landscaping works as far as practicable. Other mitigation requirements are listed below:	Project Site Area / Construction Phase	Contractor		V		√	Waste Disposal Ordinance ETWB TCW No.19/2005 DEVB TCW No. 6/2010

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		A WMP, which becomes part of the EMP, should be prepared in accordance with ETWB TCW No.19/2005;							
		A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be adopted for easy tracking; and							
		In order to monitor the disposal of C&D materials at public filling facilities and landfills and to control fly-tipping, a trip-ticket system should be adopted (refer to DEVB TCW No. 6/2010).							
		It is recommended that specific areas should be provided by the Contractors for sorting and to provide temporary storage areas (if required) for the sorted materials.							
12.6.5	11.2.5	The Contactor should prepare and implement an EMP in accordance with ETWB TCW No.19/2005, which describes the arrangements for avoidance, reuse, recovery, recycling, storage, collection, treatment and disposal of different categories of waste to be generated from construction activities. Such a management plan should incorporate site specific factors, such as the designation of areas for segregation and temporary storage of reusable and recyclable materials. The EMP should	Project Site Area / Construction Phase	Contractor		1			ETWB TCW No.19/2005

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion Sta	age ¹	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		be submitted to the Engineer for approval. The Contractor should implement waste management practices in the EMP throughout the construction stage of the Project. The EMP should be reviewed regularly and updated by the Contractor, preferably on a monthly basis.							
12.6.5	11.2.5	All surplus C&D materials arising from or in connection with construction works should become the property of the Contractor when it is removed unless otherwise stated. The Contractor would be responsible for devising a system to work for on-site sorting of C&D materials and promptly removing all sorted and process materials arising from the construction activities to minimise temporary stockpiling on-site. The system should be included in the EMP identifying the source of generation, estimated quantity, arrangement for on-site sorting, collection, temporary storage areas and frequency of collection by recycling Contractors or frequency of removal off-site.	Project Site Area / Construction Phase	Contractor		1		√ ·	-
12.6.6	11.2.6	The practices of good housekeeping for CSTW listed below should be followed to ameliorate any odour impact from handling, collection, transportation and disposal of sludge:	Operation Phases	Operator			√		Waste Disposal Ordinance

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	menta	tion Sta	age ¹	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		Screens should be cleaned regularly to remove any accumulated organic debris							
		Grit and screening transfer systems should be flushed regularly with water to remove organic debris and grit							
		Grit and screened materials should be transferred to closed containers							
		Scum and grease collection wells and troughs should be emptied and flushed regularly to prevent putrefaction of accumulated organics							
		Skim and remove floating solids and grease from primary clarifiers regularly							
		Frequent sludge withdrawal from tanks is necessary to prevent the production of gases							
		Sludge should be transported to the STF by water-tight containers to avoid Hydrogen Sulphide (H ₂ S)/odour emission and ingress of water into the containers which would lower the sludge dryness during transportation							
		Sludge cake should be transferred to closed containers							
		Sludge containers should be flushed with water regularly							

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	tion St	age 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		Sludge trucks and containers should be washed thoroughly before leaving the CSTW to avoid any odour nuisance during transportation							
12.6.6	11.2.6	In addition, all wastewater generated from the sludge dewatering process and all contaminated water from the cleaning operations recommended for odour control will be diverted to the relocated STSTW for proper treatment.	Operation Phases	Operator			V		Waste Disposal Ordinance
12.6.7	11.2.7	If chemical wastes are produced at the construction site or during operation, the Contractor during construction or the operator during operation will be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidising, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to the licensed Chemical Waste Treatment Centre, or other	Construction and Operation Phases	Contractor / Operator		V	1		Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes

EIA Ref.	EM&A Log	Environmental Protection Measures	Location / Duration of	Implementation Agent	Imple	ementa	ation S	tage 1	Relevant Legislation & Guidelines
	Ref.		Measures / Timing of Completion of Measures		Des	С	0	Dec	
		licensed facilities, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.							
12.6.8	11.2.8	Recycling of waste paper, aluminium cans and plastic bottles should be encouraged, it is recommended to place clearly labelled recycling bins at designated locations which could be accessed conveniently. Other general refuse should be separated from chemical and industrial waste by providing separated bins for storage to maximise the recyclable volume.	Construction and Operation Phases	Contractor / Operator		٧	√ 		Public Health and Municipal Services Ordinance (Cap.132)
12.6.8	11.2.8	A reputable licensed waste collector should be employed to remove general refuse on a daily basis to minimise odour, pest and litter impacts.	Construction and Operation Phases	Contractor / Operator		1	√		Public Health and Municipal Services Ordinance (Cap. 132)
	Health I	mpact							
-	-	Not applicable.							

Appendix 4.1

Action and Limit Level

Action and Limit Level

Action and Limit Level for Noise Monitoring

		Limi	t Level (dB(A))		
Monitoring Station	Action Level	0700-1900 hrs on normal weekdays	0700-2300 hrs on holidays (including Sundays); and 1900-2300 hrs on all days ²	2300-0700 hrs of all days ²	
CM1		65 / 70 ¹			
CM2(A)	When one	65 / 70 ¹			
CM3	documented complaint is	65 / 70 ¹	60 / 65 / 70 ³	45 / 50 / 55 ³	
CM4	received	75			
CM5		75			

- Remark 1: Limit level of CM1, CM2(A) and CM3 reduce to 65 dB (A) during examination periods if any.
- Remark 2: Construction noise during restricted hours is under the control of Noise Control Ordinance Limit Level to be selected based on Area Sensitivity Rating.
- Remark 3: Limit Level for restricted hour monitoring shall act as reference level only. Investigation would be conducted on CNP compliance if exceedance recorded during restricted hour noise monitoring period.

Action and Limit Level for Air Quality Monitoring

Monitoring Locations	1-hour TSP Level in μg/m3					
	Action Level	Limit Level				
AM1	294	500				
AM2	325	500				
AM3(A)	360	500				
AM4	297	500				
AM5	349	500				

Appendix 4.2

Copies of Calibration Certificates



• Device Type:

Stamp:

Manufacturer Calibration Certificate

XL2 Audio and Acoustic Analyzer

The following instrument has been tested and calibrated to the manufacturer specifications. The calibration is traceable in accordance with ISO/IEC 17025 covering all instrument functions.

Serial Number:	A2A-15360-E0
Certificate Issued:	19 February 2019
Certificate Number:	43515-A2A-15360-E0
• Deculte	DACCED
Results:	PASSED (for detailed report see next page)
Tested by:	M. Frick
Signature:	

Inh alten Riet 102 LIV 9494 Schaan www.nti-audio.com Calibration of: XL2 Audio and Acoustic Analyzer

Serial Number: A2A-15360-E0
Date: 19 February 2019

Detailed Calibration Test Results:

				actual	XL2	calibration
	reference	actual	unit	error	tolerance	uncertainty ²
R Input	0.1	0.100	V	≤0.1%	±0.5%	±0.10%
	1	1.000	V	≤0.1%	±0.5%	±0.09%
	10	9.991	V	-0.1%	±0.5%	±0.09%
20 Hz	1	0.996	V	-0.4%	±1.1%	±0.09%
20 kHz	1	1.005	V	0.5%	±1.1%	±0.09%
	1000	999.99	Hz	≤0.003%	±0.003%	±0.01%
XLR		< 2 uV			<2 uV	±0.50%
, XLR Inpu	t	-99.7	dB		typ100 dB	±0.50%
	20 kHz	R Input 0.1 1 10 20 Hz 1 20 kHz 1 1000	R Input 0.1 0.100 1 1.000 10 9.991 20 Hz 1 0.996 20 kHz 1 1.005 1000 999.99 XLR < 2 uV	R Input 0.1 0.100 V 1 1.000 V 10 9.991 V 20 Hz 1 0.996 V 20 kHz 1 1.005 V 1000 999.99 Hz XLR < 2 uV	reference actual unit error R Input 0.1 0.100 V ≤0.1% 1 1.000 V ≤0.1% 10 9.991 V -0.1% 20 Hz 1 0.996 V -0.4% 20 kHz 1 1.005 V 0.5% 1000 999.99 Hz ≤0.003% XLR < 2 uV	reference actual unit error tolerance R Input 0.1 0.100 V ≤0.1% ±0.5% 1 1.000 V ≤0.1% ±0.5% 10 9.991 V -0.1% ±0.5% 20 Hz 1 0.996 V -0.4% ±1.1% 20 kHz 1 1.005 V 0.5% ±1.1% 1000 999.99 Hz ≤0.003% ±0.003% XLR < 2 uV <2 uV

•	Test Conditions:	Temperature:	29.7	°C
		Relative Humidity:	21.7	%

• Calibration Equipment Used:

 Agilent Multimeter, Typ 34401A, Serial No. MY 5300 4607 Last calibration: 15.08.2018, Next calibration: 15.08.2019 Calibrated by ELCAL to the national standards maintained at Swiss Federal Office of Metrology. SCS 0002

FX100 Audio Analyzer, Serial No. 10408
 Last Calibration: 27.04.2018, Next Calibration: 27.04.2019
 Manufacturer calibration based on Agilent 34410, Serial No. MY47014254,
 Last Calibration: 11.05.2018, Next Calibration: 11.05.2019
 which is calibrated by ELCAL to national standards maintained at Swiss Federal Office of Metrology. SCS 002

 $^{^{1}}$ The specified tolerance +/-0.1 dB @ 1V = +/- 1.1%

² The reported expanded uncertainty is based on a standard uncertainty multiplied by a coverage factor k=2, providing a level of confidence of approximately 95%. The uncertainty evaluation has been carried out in accordance with the regulations of the GUM.



Manufacturer Calibration Certificate

The following instrument has been tested and calibrated to the manufacturer specifications. The calibration is traceable in accordance with ISO/IEC 17025 covering all instrument functions.

• Device Type: M2230 Measurement Microphone

consisting of

MA220 Serial Number: 8034 Capsule Serial Number: A16673

• Certificate Issued: 19 February 2019

• Certificate Number: 43515-8034-M2230

Results: PASSED

(for detailed report see next page)

Tested by: M.Frick

Signature:

Stamp: N7i Audio AG
Im alten Riet 102


Ll√ 9494 Schaan ww.nti-audio.com Date: 19 February 2019


Calibration of: M2230 Measurement Microphone

MA220 Serial Number: 8034 Capsule Serial Number: A16673

Detailed Calibration Test Results:

Frequency response:



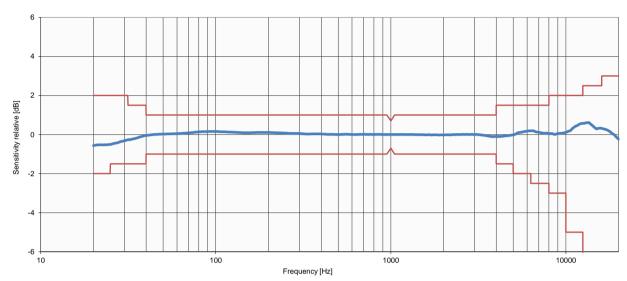

calibration actual tolerance uncertainty¹
Sensitivity @ 1 kHz, 114 dBSPL 45.5 mV/Pa 34-53 mV/Pa ±2.85%

Test Conditions:
 Temperature:
 Relative Humidity:
 Air Pressure:
 21.8 °C
 ±0.5 °C
 ±2%
 ±2%
 ±0.25 kPa

Calibration Equipment Used:

Norsonic Sound Calibrator, Type 1251, S/No. 30930
 Last Calibration: 05.12.2018, Next Calibration: 05.12.2020
 Calibrated by Metas, Switzerland

NTi Audio FX100, S/No. 11094
 Last Calibration: 14.08.2018, Next Calibration: 14.08.2019
 Calibrated by NTi Audio meeting product specifications

- MTG MV203, S/No. 0630 / Mic Capsule, MK221 S./No. 16502 Last Calibration: 08.12.2017, Next Calibration: 08.12.2019 Calibrated by MTG, Germany

¹ The reported expanded uncertainty is based on a standard uncertainty multiplied by a coverage factor k=2, providing a level of confidence of approximately 95%. The uncertainty evaluation has been carried out in accordance with the regulations of the GUM.



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. Website: www.cigismec.com E-mail: smec@cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Certificate No.:

20CA0214 01-01

Page

2

Item tested

Description: Manufacturer:

Sound Level Meter (Type 1) Nti

Microphone Nti Andio

Preamp Nti Andio

Type/Model No.:

XI2

MC230A

MA220

Serial/Equipment No.: Adaptors used:

A2A-15360-EO

A16673

8034

Item submitted by

Customer Name:

Lam Environmental Services Limited.

Address of Customer:

Request No .: Date of receipt:

14-Feb-2020

Date of test:

17-Feb-2020

Reference equipment used in the calibration

Description:

Multi function sound calibrator

Model:

Serial No.

Expiry Date:

Traceable to:

B&K 4226

2288444

23-Aug-2020

CIGISMEC

Signal generator

DS 360

33873

10-May-2020

CEPREI

Ambient conditions

Temperature:

21 ± 1 °C

Relative humidity: Air pressure:

55 ± 10 % 1000 ± 5 hPa

Test specifications

The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 1, and the lab calibration procedure SMTP004-CA-152.

2. The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.

The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference 3. between the free-field and pressure responsess of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Fend

Approved Signatory:

Date:

18-Feb-2020

Company Chop:

The results reported hat his certificate refer to the condition of the instrument on the date of calibration and Comments: carry no implication regarding the long-term stability of the instrument.

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-1/Issue 1/Rev.C/01/02/2007



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

20CA0214 01-01

Page

2

2

1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
_155.0				
Self-generated noise	Α	Pass	0.3	
9	С	Pass	0.8	2.1
	Lin	Pass	1.6	2.2
Linearity range for Leq	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	Α	Pass	0.3	
	С	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	Pass	0.3	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/10 ³ at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 ⁴ at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

2. Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
	Weighting A at 8000 Hz	Pass	0.5	

3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

End

Date:

Fung Chi Yip 7-Feb-2020 Checked by:

Date:

Shek Kwong Tat 18-Feb-2020

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-2/Issue 1/Rev.C/01/02/2007



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 1 of 6

Sound level meter type:

XL2

Serial No.

A2A-15360-EO Date

17-Feb-2020

Microphone

type:

MC230A

Serial No.

A16673

Report: 20CA0214 01-01

SELF GENERATED NOISE TEST

The noise test is performed in the most sensitive range of the SLM with the microphone replaced by an equivalent impedance.

Noise level in A weighting 17.8 dB
Noise level in C weighting 18.0 dB
Noise level in Lin 23.3 dB

LINEARITY TEST

The linearity is tested relative to the reference sound pressure level using a continuous sinusoidal signal of frequency 4 kHz. The measurement is made on the reference range for indications at 5 dB intervals starting from the 94 dB reference sound pressure level. And until within 5 dB of the upper and lower limits of the reference range, the measurements shall be made at 1 dB intervals.(SLM set to LEQ/SPL)

Reference/Expected level	Actua	ıl level	Tolerance	Devia	ation
Neierence/Expected rever	non-integrated	integrated		non-integrated	integrated
dB	dB	dB	+/- dB	dB	dB
94.0	94.0	94.0	0.7	0.0	0.0
99.0	99.0	99.0	0.7	0.0	0.0
104.0	104.0	104.0	0.7	0.0	0.0
109.0	109.0	109.0	0.7	0.0	0.0
114.0	114.0	114.0	0.7	0.0	0.0
115.0	115.0	115.0	0.7	0.0	0.0
116.0	116.0	116.0	0.7	0.0	0.0
117.0	117.0	117.0	0.7	0.0	0.0
118.0	118.0	118.0	0.7	0.0	0.0
119.0	119.0	119.0	0.7	0.0	0.0
120.0	120.0	120.0	0.7	0.0	0.0
89.0	89.0	89.0	0.7	0.0	0.0
84.0	84.0	84.0	0.7	0.0	0.0
79.0	79.0	79.0	0.7	0.0	0.0
74.0	74.0	74.0	0.7	0.0	0.0
69.0	69.0	69.0	0.7	0.0	0.0
64.0	64.0	64.0	0.7	0.0	0.0
59.0	59.0	59.0	0.7	0.0	0.0
54.0	54.0	54.0	0.7	0.0	0.0
49.0	49.0	49.0	0.7	0.0	0.0
44.0	44.0	44.0	0.7	0.0	0.0
39.0	39.0	39.0	0.7	0.0	0.0
34.0	34.1	34.1	0.7	0.1	0.1
33.0	33.1	33.1	0.7	0.1	0.1



香港 黄 竹 坑 道 3 7 號 利 達 中 心 1 2 樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 2 of 6

Sound level me		XL2		Serial No.	A2A-15360-EO	Date 17-Fe	b-2020
Microphone	type:	MC230A		Serial No.	A16673	Report: 20CAC	214 01-01
32.0		32.2	32.2	0.7	0.2	0.2	
31.0		31.2	31.2	0.7	0.2	0.2	
30.0		30.3	30.3	0.7	0.3	0.3	

Measurements for an indication of the reference SPL on all other ranges which include it

Other ranges	Expected level	Actual level	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
40-140	94.0	94.0	0.7	0.0
20-120	94.0	94.0	0.7	0.0
0-100	94.0	94.0	0.7	0.0

Measurements on all level ranges for indications 2 dB below the upper limit and 2 dB above the lower limit

Ranges	Reference/Expected level	Actual level	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
40.140	52.0	52.5	0.7	0.5
40-140	138.0	138.0	0.7	0.0
20.120	30.0	30.3	0.7	0.3
20-120	118.0	118.0	0.7	0.0
0.100	30.0	30.0	0.7	0.0
0-100	98.0	98.0	0.7	0.0

FREQUENCY WEIGHTING TEST

The frequency response of the weighting netwoks are tested at octave intervals over the frequency ranges 31.5 Hz to 12500 Hz. The signal level at 1000 Hz is set to give an indication of the reference SPL.

Frequency weighting A:

Frequency	Ref. level	Expected level	Actual level	Tolerar	nce(dB)	Deviation
Hz	dB	dB	dB	+	-	dB
1000.0	94.0	94.0	94.0	0.0	0.0	0.0
31.6	94.0	54.6	54.4	1.5	1.5	-0.2
63.1	94.0	67.8	67.6	1.5	1.5	-0.2
125.9	94.0	77.9	77.8	1.0	1.0	-0.1
251.2	94.0	85.4	85.3	1.0	1.0	-0.1
501.2	94.0	90.8	90.7	1.0	1.0	-0.1
1995.0	94.0	95.2	95.1	1.0	1.0	-0.1
3981.0	94.0	95.0	94.9	1.0	1.0	-0.1
7943.0	94.0	92.9	92.9	1.5	3.0	0.0
12590.0	94.0	89.7	89.5	3.0	6.0	-0.2

Frequency weighting C:

Frequency	Ref. level	Expected level	Actual level	Tolerar	nce(dB)	Deviation
Hz	dB	dB	dB	+	_	dB



香港 黄 竹 坑 道 3 7 號 利 達 中 心 1 2 樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 3 of 6

Sound level me	ter type:	XL2	Serial No.	A2A	A-15360-EO	Date	17-Feb-2020
Microphone	type:	MC230A	Serial No.	A16	673		
						Report:	20CA0214 01-01
1000.0	94.0	94.0	94.0	0.0	0.0	0.0	
31.6	94.0	91.0	90.8	1.5	1.5	-0.2	
63.1	94.0	93.2	93.0	1.5	1.5	-0.2	
125.9	94.0	93.8	93.8	1.0	1.0	0.0	
251.2	94.0	94.0	93.9	1.0	1.0	-0.1	
501.2	94.0	94.0	94.0	1.0	1.0	0.0	
1995.0	94.0	93.8	93.8	1.0	1.0	0.0	
3981.0	94.0	93.2	93.2	1.0	1.0	0.0	
7943.0	94.0	91.0	91.0	1.5	3.0	0.0	
12590.0	94.0	87.8	87.6	3.0	6.0	-0.2	

Frequency weighting Lin:

Frequency	Ref. level	Expected level	Actual level	Tolerar	nce(dB)	Deviation
Hz	dB	dB	dB	+	-	dB
1000.0	94.0	94.0	94.0	0.0	0.0	0.0
31.6	94.0	94.0	93.8	1.5	1.5	-0.2
63.1	94.0	94.0	93.8	1.5	1.5	-0.2
125.9	94.0	94.0	93.9	1.0	1.0	-0.1
251.2	94.0	94.0	93.9	1.0	1.0	-0.1
501.2	94.0	94.0	93.9	1.0	1.0	-0.1
1995.0	94.0	94.0	93.9	1.0	1.0	-0.1
3981.0	94.0	94.0	94.0	1.0	1.0	0.0
7943.0	94.0	94.0	94.0	1.5	3.0	0.0
12590.0	94.0	94.0	94.0	3.0	6.0	0.0

Note: No corrections for the frequency response of the microphone, instrument case and windshield are made to the sound level meter.

TIME WEIGHTING FAST TEST

Time weighting F is tested on the reference range with a single sinusoidal burst of duration 200 ms at a frequency 2000 Hz and an amplitude which produces an indication 4 dB below the upper limit of the primary indicator range when the signal is continuous. (Weight A, Maximum hold)

Ref. level	Expected level	Actual level	Tolera	nce(dB)	Deviation
dB	dB	dB	+	-	dB
116.0	115.0	115.0	1.0	1.0	0.0

TIME WEIGHTING SLOW TEST

Time weighting S is tested on the reference range with a single sinusoidal burst of duration 500 ms at a frequency 2000 Hz and an amplitude which produces an indication 4 dB below the upper limit of the primary indicator range when the signal is continuous. (Weight A. Maximum hold)

Whom the digital to continuous.	(Toigner t, maxim				
Ref. level	Expected level	Actual level	Tolera	nce(dB)	Deviation
dB	dB	dB	+	-	dB
116.0	111.9	112.0	1.0	1.0	0.1

(c)Soils Materials Eng. Co., Ltd. Form No.: CAWS 152/Issue I/Rev. B/01/02/2007



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533 SMECLab

Test Data for Sound Level Meter

Page 4 of 6

Sound level meter type:

XL2

Serial No.

A2A-15360-EO Date

17-Feb-2020

Microphone

type:

MC230A

Serial No.

A16673

Report: 20CA0214 01-01

PEAK RESPONSE TEST

The onset time of the peak detector is tested on the reference range by comparing the response to a 100 us rectangular test pulse with the response to a 10 ms reference pulse of the same amplitude. The amplitude of the 10 ms reference pulse is such as to produce an indication 1 dB below the upper limit of the primary indicator range.

Positive polarities: (Weighting Z, set the generator signal to single, Lzpeak)

Ref. level	Response to 10 ms	Response to 100 us	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
119.0	119.0	119.2	2.0	0.2

Negative polarities:

Ref. level	Response to 10 ms	Response to 100 us	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
119.0	119.0	119.2	2.0	0.2

RMS ACCURACY TEST

The RMS detector accuracy is tested on the reference range for a crest factor of 3.

Test frequency:

2000 Hz Amplitude:

Burst repetition frequency:

2 dB below the upper limit of the primary indicator range. 40 Hz

11 cycles of a sine wave of frequency 2000 Hz. Tone burst signal: Deviation Ref. Level Expected level Tone burst signal Tolerance indication(dB) +/- dB dB Time wighting dB dB Slow 0.5 0.0 118.0+6.6 118.0 118.0

TIME WEIGHTING IMPULSE TEST

Time weighting I is tested on the reference range (Set the SLM to LAImax)

Test frequency:

2000 Hz

Amplitude:

The upper limit of the primary indicator range.

Single sinusoidal burst of duration 5 ms:

Ref. Level	Single burs	t indication	Tolerance	Deviation
dB	Expected (dB)	Actual (dB)	+/- dB	dB
120.0	111.2	111.0	2.0	-0.2

Repeated at 100 Hz

Ref. Level	Repeated burst indication Tolerance D			Deviation
dB	Expected (dB)	Actual (dB)	+/- dB	dB
120.0	117.3	117.1	1.0	-0.2

TIME AVERAGING TEST

This test compares the SLM reading for continuous sine signals with readings obtained from a sine tone burst sequence having the same RMS level. The test level is 30 dB below the upper limit of the linearity range and repeated for Type 1 SLM with 40 dB below the upper limit of the linearity.

Frequency of tone burst:

4000 Hz

Duration of tone burst:

1 ms

Repetition Time	Level of	Expected	Actual	Tolerance	Deviation	Remarks
	tone burst	Leq	Leq			

Form No.: CAWS 152/Issue 1/Rev. B/01/02/2007



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 5 of 6

Sound level meter type:

XL2

Serial No. Serial No. A2A-15360-EO Date

17-Feb-2020

Microphone

type:

MC230A

A16673

Report: 20CA0214 01-01

msec	dB	dB	dB	+/- dB	dB	
1000	90.0	90.0	90.0	1.0	0.0	60s integ.
10000	80.0	80.0	79.9	1.0	-0.1	6min. integ.

PULSE RANGE AND SOUND EXPOSURE LEVEL TEST

The test tone burst signal is superimposed on a baseline signal corresponding to the lower limit of reference range

Test frequency:

4000 Hz

Integration time:

10 sec

The integrating sound level meter set to Leg:

Duration	Rms level of	Expected	Actual	Tolerance	Deviation	
msec	tone burst (dB)	dB	dB	+/- dB	dB	
10	88.0	58.0	58.0	1.7	0.0	

The integrating sound level meter set to SEL:

Duration	Rms level of	Expected	Actual	Tolerance	Deviation
msec	tone burst (dB)	dB	dB	+/- dB	dB
10.0	88.0	68.0	68.0	1.7	0.0

OVERLOAD INDICATION TEST

For SLM capable of operating in a non-integrating mode.

Test frequency:

2000 Hz

Amplitude:

2 dB below the upper limit of the primary indicator range.

Burst repetition frequency:

40 Hz

Tone burst signal:

11 cycles of a sine wave of frequency 2000 Hz.

Level	Level reduced by	Further reduced	Difference	Tolerance	Deviation
at overload (dB)	1 dB	3 dB	dB	dB	dB
121.1	120.1	117.1	3.0	1.0	0.0

For integrating SLM, with the instrument indicating Leq.

For integrating SLM, with the instrument indicating Leq and set to the reference range. The test signal as following: The test tone burst signal is superimposed on a baseline signal corresponding to the lower limit of reference range

Test frequency:

4000 Hz

Integration time:

10 sec

Single burst duration:

1 msec

Rms level	Level reduced by	Expected level	Actual level	Tolerance	Deviation
at overload (dB)	1 dB	dB	dB	dB	dB
127.1	126.1	86.1	86.1	2.2	0.0

ACOUSTIC TEST

The acoustic test of the complete SLM is tested at the frequency 125 Hz and 8000 Hz using a B&K type 4226 Multifunction Acoustic Calibrator. The test is performed in A weighting.

Frequency	Expected level	Actual level	Toleran	ce (dB)	Deviation
Hz	dB	Measured (dB)	+	-	dB

(c)Soils Materials Eng. Co., Ltd. Form No.: CAWS 152/Issue 1/Rev. B/01/02/2007



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533

SMECLab

Test Data for Sound Level Meter

Page 6 of 6

Sound level me	eter type:	XL2	Se	rial No.	A2A	A-15360-EO	Date	17-Feb-2020
Microphone	type:	MC230A	Se	rial No.	A16	6673	Report:	20CA0214 01-01
1000	94.0		94.0		0.0	0.0	0.0	
125	77.9		77.9		1.0	1.0	0.0	
8000	92.9		93.0		1.5	3.0	0.1	

-----END-----



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Certificate No.:

19CA1127 02

Page

of

2

Item tested

Description: Manufacturer: Sound Level Meter (Type 1)

Microphone

B&K

Type/Model No.:

2236 2100736 4188 2288941

Serial/Equipment No.: Adaptors used:

Item submitted by

Customer Name:

Lam Environmental Service Ltd.

Address of Customer:

Request No .: Date of receipt:

27-Nov-2019

Date of test:

29-Nov-2019

Reference equipment used in the calibration

Description:

Serial No.

Expiry Date:

Traceable to:

Multi function sound calibrator

Model: B&K 4226

2288444

23-Aug-2020

CIGISMEC

Signal generator

DS 360

61227

26-Dec-2019

CEPREI

Ambient conditions

Temperature: Air pressure:

21 ± 1 °C

Relative humidity:

55 ± 10 % 1000 ± 5 hPa

Test specifications

The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 1. and the lab calibration procedure SMTP004-CA-152.

2, The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.

3, The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Feng Jungi

Approved Signatory:

Date:

29-Nov-2019

Company Chop:

The results reported in this certificate refer to the condition of the instrument on the date of calibration and Comments: carry no implication regarding the long-term stability of the instrument.

© Soils & Materials Engineering Co., Ltd

Form No.CARP152-1/Issue 1/Rev.C/01/02/2007



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. Website: www.cigismec.com E-mail: smec@cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

19CA1127 02

Page

of

2

1, **Electrical Tests**

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	
con generated noise	C	Pass	1.0	2.1
	Lin	Pass	2.0	2.2
Linearity range for Leq	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	Α	Pass	0.3	
. , , ,	С	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	Pass	0.3	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/10 ³ at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 ⁴ at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

Acoustic tests 2,

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
	Weighting A at 8000 Hz	Pass	0.5	

3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

Fung Chi Yip

End

Checked by:

Shek Kwong Tat

Date:

29-Nov-2019

Date:

29-Nov-2019

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-2/Issue 1/Rev.C/01/02/2007



香港 黄 竹 坑 道 3 7 號 利 達 中 心 1 2 樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 1 of 6

Sound level meter type:

2236

Serial No.

2100736

Date

29-Nov-2019

Microphone

type:

4188

Serial No.

2288941

Report: 19CA1127 02

SELF GENERATED NOISE TEST

The noise test is performed in the most sensitive range of the SLM with the microphone replaced by an equivalent impedance.

Noise level in A weighting

< 20. 0

dB

Noise level in C weighting

21.0

dB

Noise level in Lin

26.5

dB

LINEARITY TEST

The linearity is tested relative to the reference sound pressure level using a continuous sinusoidal signal of frequency 4 kHz. The measurement is made on the reference range for indications at 5 dB intervals starting from the 94 dB reference sound pressure level. And until within 5 dB of the upper and lower limits of the reference range, the measurements shall be made at 1 dB intervals.(SLM set to LEQ/SPL)

Reference/Expected level	Actua	l level	Tolerance	Devia	ation
Neierence/Expected level	non-integrated	integrated		non-integrated	integrated
dB	dB	dB	+/- dB	dB	dB
94.0	94.0	94.0	0.7	0.0	0.0
99.0	99.0	99.0	0.7	0.0	0.0
104.0	104.0	104.0	0.7	0.0	0.0
109.0	109.0	109.0	0.7	0.0	0.0
114.0	114.0	114.0	0.7	0.0	0.0
119.0	119.0	119.0	0.7	0.0	0.0
124.0	123.9	123.9	0.7	-0.1	-0.1
125.0	124.9	124.9	0.7	-0.1	-0.1
126.0	125.9	125.9	0.7	-0.1	-0.1
127.0	126.9	126.9	0.7	-0.1	-0.1
128.0	127.9	127.9	0.7	-0.1	-0.1
129.0	128.9	128.9	0.7	-0.1	-0.1
130.0	129.8	129.8	0.7	-0.2	-0.2
89.0	89.0	89.0	0.7	0.0	0.0
84.0	84.1	84.1	0.7	0.1	0.1
79.0	79.0	79.0	0.7	0.0	0.0
74.0	74.1	74.1	0.7	0.1	0.1
69.0	69.0	69.0	0.7	0.0	0.0
64.0	64.0	64.0	0.7	0.0	0.0
59.0	59.0	59.0	0.7	0.0	0.0
54.0	54.0	54.0	0.7	0.0	0.0
53.0	53.0	53.0	0.7	0.0	0.0
52.0	52.1	52.1	0.7	0.1	0.1
51.0	51.1	51.1	0.7	0.1	0.1



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 2 of 6

Sound level meter type:

2236

Serial No.

2100736

Date 29-Nov-2019

Microphone

type:

4188

Serial No.

2288941

Report: 19CA1127 02

50.0 50.2 50.2 0.7 0.2 0.2

Measurements for an indication of the reference SPL on all other ranges which include it

Other ranges	Expected level	Actual level	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
60-140	94.0	94.1	0.7	0.1
50-130	94.0	94.0	0.7	0.0
40-120	94.0	93.9	0.7	-0.1
30-110	94.0	93.9	0.7	-0.1
20-100	94.0	93.9	0.7	-0.1

Measurements on all level ranges for indications 2 dB below the upper limit and 2 dB above the lower limit

Ranges	Reference/Expected level	Actual level	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
60-140	62.0	62.1	0.7	0.1
00-140	138.0	137.8	0.7	-0.2
50-130	52.0	52.1	0.7	0.1
30-130	128.0	127.9	0.7	-0.1
40-120	42.0	42.1	0.7	0.1
40-120	118.0	117.9	0.7	-0.1
30-110	32.0	32.2	0.7	0.2
30-110	108.0	107.9	0.7	-0.1
20-100	30.0	30.1	0.7	0.1
20-100	98.0	97.9	0.7	-0.1

FREQUENCY WEIGHTING TEST

The frequency response of the weighting netwoks are tested at octave intervals over the frequency ranges 31.5 Hz to 12500 Hz. The signal level at 1000 Hz is set to give an indication of the reference SPL.

Frequency weighting A:

Frequency	Ref. level	Expected level	Actual level	Tolerar	nce(dB)	Deviation
Hz	dB	dB	dB	+	-	dB
1000.0	94.0	94.0	94.0	0.0	0.0	0.0
31.6	94.0	54.6	54.6	1.5	1.5	0.0
63.1	94.0	67.8	67.8	1.5	1.5	0.0
125.9	94.0	77.9	77.9	1.0	1.0	0.0
251.2	94.0	85.4	85.4	1.0	1.0	0.0
501.2	94.0	90.8	90.8	1.0	1.0	0.0
1995.0	94.0	95.2	95.2	1.0	1.0	0.0
3981.0	94.0	95.0	95.0	1.0	1.0	0.0
7943.0	94.0	92.9	92.9	1.5	3.0	0.0



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 3 of 6

Sound level meter type:

2236

Serial No.

2100736

Date

29-Nov-2019

Microphone

type:

4188

Serial No.

2288941

Report: 19CA1127 02

12590.0 94.0 89.7 89.6 3.0 6.0 -0.1

Frequency weighting C:

Frequency	Ref. level	Expected level	Actual level	Tolera	nce(dB)	Deviation
Hz	dB	dB	dB	+	-	dB
1000.0	94.0	94.0	94.0	0.0	0.0	0.0
31.6	94.0	91.0	91.0	1.5	1.5	0.0
63.1	94.0	93.2	93.2	1.5	1.5	0.0
125.9	94.0	93.8	93.9	1.0	1.0	0.1
251.2	94.0	94.0	94.0	1.0	1.0	0.0
501.2	94.0	94.0	94.1	1.0	1.0	0.1
1995.0	94.0	93.8	93.9	1.0	1.0	0.1
3981.0	94.0	93.2	93.2	1.0	1.0	0.0
7943.0	94.0	91.0	91.0	1.5	3.0	0.0
12590.0	94.0	87.8	87.8	3.0	6.0	0.0

Frequency weighting Lin:

Frequency	Ref. level	Expected level	Actual level	Tolerar	nce(dB)	Deviation
Hz	dB	dB	dB	+	-	dB
1000.0	94.0	94.0	94.0	0.0	0.0	0.0
31.6	94.0	94.0	94.0	1.5	1.5	0.0
63.1	94.0	94.0	94.0	1.5	1.5	0.0
125.9	94.0	94.0	94.0	1.0	1.0	0.0
251.2	94.0	94.0	93.9	1.0	1.0	-0.1
501.2	94.0	94.0	93.9	1.0	1.0	-0.1
1995.0	94.0	94.0	93.9	1.0	1.0	-0.1
3981.0	94.0	94.0	94.0	1.0	1.0	0.0
7943.0	94.0	94.0	94.1	1.5	3.0	0.1
12590.0	94.0	94.0	94.2	3.0	6.0	0.2

TIME WEIGHTING FAST TEST

Time weighting F is tested on the reference range with a single sinusoidal burst of duration 200 ms at a frequency 2000 Hz and an amplitude which produces an indication 4 dB below the upper limit of the primary indicator range when the signal is continuous. (Weight A, Maximum hold)

Ref. level	Expected level	Expected level Actual level Tolerance(dB)	Tolerance(dB)		Deviation
dB	dB	dB	+	-	dB
109.0	108.0	108.1	1.0	1.0	0.1

TIME WEIGHTING SLOW TEST

Time weighting S is tested on the reference range with a single sinusoidal burst of duration 500 ms at a frequency 2000 Hz and an amplitude which produces an indication 4 dB below the upper limit of the primary indicator range when the signal is continuous. (Weight A, Maximum hold)

Ref. level	Expected level	Actual level	Tolerance(dB)	Deviation
dB	dB	dB	+ -	dB



綜 台 試 驗 甭 限 公 司 SOILS & MATERIALS ENGINEERING CO., LTD.

港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533

SMECLab

Test Data for Sound Level Meter

Page 4 of 6

Sound level meter type:

2236

Serial No.

2100736

Date 29-Nov-2019

Microphone

type:

4188

Serial No.

2288941

Report: 19CA1127 02

109.0

-0.1

104.9 104.8 1.0 1.0

PEAK RESPONSE TEST

The onset time of the peak detector is tested on the reference range by comparing the response to a 100 us rectangular test pulse with the response to a 10 ms reference pulse of the same amplitude. The amplitude of the 10 ms reference pulse is such as to produce an indication 1 dB below the upper limit of the primary indicator range.

Positive polarities:

(Weighting L. set the generator signal to single, LLPeak)

Ref. level	Response to 10 ms	Response to 100 us	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
112.0	112.0	112.1	2.0	0.1

Negative polarities:

Ref. level	Response to 10 ms	Response to 100 us	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
112.0	112.0	112.1	2.0	0.1

RMS ACCURACY TEST

The RMS detector accuracy is tested on the reference range for a crest factor of 3.

Test frequency:

2000 Hz

Amplitude:

2 dB below the upper limit of the primary indicator range.

Burst repetition frequency:

Tone burst signal:

11 cycles of a sine wave of frequency 2000 Hz. (Set to INT)

	Ref. Level	Expected level	Tone burst signal	Tolerance	Deviation
Time wighting	dB	dB	indication(dB)	+/- dB	dB
Slow	111.0+6.6	111.0	110.8	0.5	-0.2

TIME WEIGHTING IMPULSE TEST

Time weighting I is tested on the reference range (Set the SLM to LAImax)

Test frequency:

2000 Hz

Amplitude:

The upper limit of the primary indicator range.

Single sinusoidal burst of duration 5 ms:

Ref. Level	Single burs	Single burst indication		Deviation
dB	Expected (dB)	Actual (dB)	+/- dB	dB
113.0	104.2	104.1	2.0	-0.1

Repeated at 100 Hz

Ref. Level	Repeated burst indication		Tolerance	Deviation
dB	Expected (dB)	Actual (dB)	+/- dB	dB
113.0	110.3	110.2	1.0	-0.1

TIME AVERAGING TEST

This test compares the SLM reading for continuous sine signals with readings obtained from a sine tone burst sequence having the same RMS level. The test level is 30 dB below the upper limit of the linearity range and repeated for Type 1 SLM with 40 dB below the upper limit of the linearity.

Frequency of tone burst:

4000 Hz

Duration of tone burst:

1 ms



香港 黄竹坑 道 3 7 號 利 達 中 心 1 2 樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 5 of 6

Sound level meter type:

2236

Serial No.

2100736

Date

29-Nov-2019

Microphone

type:

4188

Serial No.

2288941

Report: 19CA1127 02

Repetition Time	Level of	Expected	Actual	Tolerance	Deviation	Remarks
	tone burst	Leq	Leq			
msec	dB	dB	dB	+/- dB	dB	
1000	100.0	100.0	99.6	1.0	-0.4	60s integ.
10000	90.0	90.0	89.3	1.0	-0.7	6min. integ

PULSE RANGE AND SOUND EXPOSURE LEVEL TEST

The test tone burst signal is superimposed on a baseline signal corresponding to the lower limit of reference range

Test frequency:

4000 Hz

Integration time:

10 sec

The integrating sound level meter set to Leq:

Duration	Rms level of	Expected	Actual	Tolerance	Deviation
msec	tone burst (dB)	dB	dB	+/- dB	dB
10	116.0	86.0	85.8	1.7	-0.2

The integrating sound level meter set to SEL:

Duration	Rms level of	Expected	Actual	Tolerance	Deviation
msec	tone burst (dB)	dB	dB	+/- dB	dB
10.0	116.0	96.0	95.9	1.7	-0.1

OVERLOAD INDICATION TEST

For SLM capable of operating in a non-integrating mode.

Test frequency:

2000 Hz

Amplitude:

2 dB below the upper limit of the primary indicator range.

Burst repetition frequency:

40 Hz

Tone burst signal:

11 cycles of a sine wave of frequency 2000 Hz.

Level	Level reduced by	Further reduced	Difference	Tolerance	Deviation
at overload (dB)	1 dB	3 dB	dB	dB	dB
126.0	125.0	122.0	3.0	1.0	0.0

For integrating SLM, with the instrument indicating Leq.

For integrating SLM, with the instrument indicating Leq and set to the reference range. The test signal as following: The test tone burst signal is superimposed on a baseline signal corresponding to the lower limit of reference range

Test frequency:

4000 Hz

Integration time:

10 sec 1 msec

1111	.cgi	ation	tillio.			10
Sii	ngle	burs	t dura	atio	n:	1 n
_						

Rms level	Level reduced by	Expected level	Actual level	Tolerance	Deviation
at overload (dB)	1 dB	dB	dB	dB	dB
130.6	129.6	89.6	89.4	2.2	-0.2

ACOUSTIC TEST

The acoustic test of the complete SLM is tested at the frequency 125 Hz and 8000 Hz using a B&K type 4226 Multifunction Acoustic Calibrator. The test is performed in A weighting.



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 6 of 6

Sound level meter type:

2236

Serial No.

2100736

Date

29-Nov-2019

Microphone

type:

4188

Serial No.

2288941

Report: 19CA1127 02

Frequency	Expected level	Actual level	Tolerar	Tolerance (dB)	
Hz	dB	Measured (dB)	+	-	dB
1000	94.0	94.0	0.0	0.0	0.0
125	77.9	78.0	1.0	1.0	0.1
8000	92.9	93.5	1.5	3.0	0.6

-----END-----



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533





CERTIFICATE OF CALIBRATION

Certificate No.:

19CA0329 01

Page

1

2

Item tested

Description: Manufacturer: Sound Level Meter (Class 1)

Microphone

....

Type/Model No.: Serial/Equipment No.: Honglim Co., Ltd. HLES-01 201692136

CDM101

CDM10 05866

Adaptors used:

_

_

Item submitted by

Customer Name:

Lam Environmental Service Ltd.

Address of Customer:

-

Request No.: Date of receipt:

29-Mar-2019

Date of test:

02-Apr-2019

Reference equipment used in the calibration

Description:

Model: B&K 4226 Serial No.

Expiry Date:

Traceable to:

Multi function sound calibrator Signal generator Signal generator

DS 360 DS 360 2288444 33873 61227 23-Aug-2019 24-Apr-2019 26-Dec-2019 CIGISMEC CEPREI CEPREI

Ambient conditions

Temperature:

21 ± 1 °C 55 ± 10 %

Relative humidity: Air pressure:

1005 ± 5 hPa

Test specifications

1, The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.

2, The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.

3, The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Fend Junai

Approved Signatory:

Date:

02-Apr-2019

Company Chop:

SENGINESHING COMMON TRANSPORTER

Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-1/Issue 1/Rev C/01/02/2007



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

19CA0329 01

Page

Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	
	С	Pass	0.8	2.1
	Lin	N/A	N/A	
Linearity range for Leq	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	A	Pass	0.3	
	С	Pass	0.3	
	Lin	N/A	N/A	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	N/A	N/A	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	N/A	N/A	
	Repeated at frequency of 100 Hz	N/A	N/A	
Time averaging	1 ms burst duty factor 1/10 ³ at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 ⁴ at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	N/A	N/A	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Weighting A at 125 Hz	Pass	0.3	
Weighting A at 8000 Hz	Pass	0.5	
	Weighting A at 125 Hz	Weighting A at 125 Hz Pass	SubtestStatusUncertanity (dB)Weighting A at 125 HzPass0.3

3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

Checked by:

Fung Chi

Date:

Fong Chun Wai

The standard(s) and equipment used in the calibration are traceable to national dr international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-2/Issue 1/Rev.C/01/02/2007



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 1 of 4

Sound level meter type:

HLES-01

Serial No.

201692136

Date 02-Apr-2019

Microphone

type:

CDM101 Serial No.

05866

Report: 19CA0329 01

SELF GENERATED NOISE TEST

The noise test is performed in the most sensitive range of the SLM with the microphone replaced by an equivalent impedance.

Noise level in A weighting

17.7

dB

Noise level in C weighting

20.5

dB

LINEARITY TEST

The linearity is tested relative to the reference sound pressure level using a continuous sinusoidal signal of frequency 4 kHz. The measurement is made on the reference range for indications at 5 dB intervals starting from the 94 dB reference sound pressure level. And until within 5 dB of the upper and lower limits of the reference range, the measurements shall be made at 1 dB intervals.(SLM set to LEQ/SPL)

Reference/Expected level	Actual level		Tolerance	Deviation		
Neierence/Expedied lever	non-integrated	integrated		non-integrated	integrated	
dB	dB	dB	+/- dB	dB	dB	
94.0	94.0	94.0	0.7	0.0	0.0	
99.0	99.0	99.0	0.7	0.0	0.0	
104.0	104.0	104.0	0.7	0.0	0.0	
109.0	109.1	109.1	0.7	0.1	0.1	
110.0	110.1	110.1	0.7	0.1	0.1	
111.0	111.1	111.1	0.7	0.1	0.1	
112.0	112.1	112.1	0.7	0.1	0.1	
113.0	113.1	113.1	0.7	0.1	0.1	
114.0	113.9	113.9	0.7	-0.1	-0.1	
115.0	114.4	114.4	0.7	-0.6	-0.6	
89.0	89.0	89.0	0.7	0.0	0.0	
84.0	84.0	84.0	0.7	0.0	0.0	
79.0	79.0	79.0	0.7	0.0	0.0	
74.0	73.9	73.9	0.7	-0.1	-0.1	
69.0	68.9	68.9	0.7	-0.1	-0.1	
64.0	63.9	63.9	0.7	-0.1	-0.1	
59.0	58.9	58.9	0.7	-0.1	-0.1	
54.0	53.9	53.9	0.7	-0.1	-0.1	
49.0	49.0	49.0	0.7	0.0	0.0	
48.0	48.0	48.0	0.7	0.0	0.0	
47.0	46.8	46.8	0.7	-0.2	-0.2	
46.0	45.8	45.8	0.7	-0.2	-0.2	
45.0	44.9	44.9	0.7	-0.1	-0.1	

Measurements for an indication of the reference SPL on all other ranges which include it



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533

SMECLab

Test Data for Sound Level Meter

Page 2 of 4

Sound level meter type:

rpe: F

HLES-01

Serial No.

201692136

Date 02

02-Apr-2019

Microphone

type:

CDM101

Serial No.

05866

Report: 19CA0329 01

Other ranges	Expected level	Actual level	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
65-135	94.0	94.0	0.7	0.0
45-115	94.0	94.0	0.7	0.0
25-95	94.0	94.0	0.7	0.0

Measurements on all level ranges for indications 2 dB below the upper limit and 2 dB above the lower limit

Ranges	Reference/Expected level	Actual level	Tolerance	Deviation
dB	dB	dB	+/- dB	dB
65-135	67.0	67.2	0.7	0.2
03-133	133.0	133.3	0.7	0.3
45-115	47.0	46.8	0.7	-0.2
45-115	113.0	113.1	0.7	0.1
25-95	27.0	27.2	0.7	0.2
25-95	93.0	93.2	0.7	0.2

FREQUENCY WEIGHTING TEST

The frequency response of the weighting netwoks are tested at octave intervals over the frequency ranges 31.5 Hz to 12500 Hz. The signal level at 1000 Hz is set to give an indication of the reference SPL.

Frequency weighting A:

Frequency	Ref. level	Expected level	Actual level	Tolerar	nce(dB)	Deviation
Hz	dB	dB	dB	+	-	dB
1000.0	94.0	94.0	94.0	0.0	0.0	0.0
31.6	94.0	54.6	54.1	1.5	1.5	-0.5
63.1	94.0	67.8	67.3	1.5	1.5	-0.5
125.9	94.0	77.9	77.6	1.0	1.0	-0.3
251.2	94.0	85.4	85.1	1.0	1.0	-0.3
501.2	94.0	90.8	90.6	1.0	1.0	-0.2
1995.0	94.0	95.2	95.3	1.0	1.0	0.1
3981.0	94.0	95.0	95.2	1.0	1.0	0.2
7943.0	94.0	92.9	93.3	1.5	3.0	0.4
12590.0	94.0	89.7	90.8	3.0	6.0	1.1

Frequency weighting C:

Frequency	Ref. level	Expected level	Actual level	Tolerar	nce(dB)	Deviation
Hz	dB	dB	dB	+	-	dB
1000.0	94.0	94.0	94.0	0.0	0.0	0.0
31.6	94.0	91.0	90.4	1.5	1.5	-0.6
63.1	94.0	93.2	92.7	1.5	1.5	-0.5
125.9	94.0	93.8	93.6	1.0	1.0	-0.2
251.2	94.0	94.0	93.8	1.0	1.0	-0.2



香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533

SMECLab

Test Data for Sound Level Meter

Page 3 of 4

Sound level me	eter type:	HLES-01	Serial No.	201	692136	Date	02-Apr-2019
Microphone	type:	CDM101	Serial No.	058	66		
						Report:	19CA0329 01
501.2	94.0	94.0	93.9	1.0	1.0	-0.1	
1995.0	94.0	93.8	93.8	1.0	1.0	0.0	
3981.0	94.0	93.2	93.3	1.0	1.0	0.1	
7943.0	94.0	91.0	91.3	1.5	3.0	0.3	
12590.0	94.0	87.8	88.7	3.0	6.0	0.9	

Note: No corrections for the frequency response of the microphone, instrument case and windshield are made to the sound level meter.

TIME WEIGHTING FAST TEST

Time weighting F is tested on the reference range with a single sinusoidal burst of duration 200 ms at a frequency 2000 Hz and an amplitude which produces an indication 4 dB below the upper limit of the primary indicator range when the signal is continuous. (Weight A. Maximum hold)

mineral and organization derital and a	(110.9.11)	,				
Ref. level	Ref. level Expected level		Tolerance(dB)		Deviation	
dB	dB	dB	+	-	dB	
111.0	110.0	109.9	1.0	1.0	-0.1	

TIME WEIGHTING SLOW TEST

Time weighting S is tested on the reference range with a single sinusoidal burst of duration 500 ms at a frequency 2000 Hz and an amplitude which produces an indication 4 dB below the upper limit of the primary indicator range when the signal is continuous. (Weight A, Maximum hold)

Ref. level	Ref. level Expected level		Tolerance(dB)		Deviation	
dB	dB	dB	+	-	dB	
, 111.0	106.9	106.8	1.0	1.0	-0.1	

RMS ACCURACY TEST

The RMS detector accuracy is tested on the reference range for a crest factor of 3.

Test frequency:

2000 Hz

Amplitude:

2 dB below the upper limit of the primary indicator range.

Burst repetition frequency:

40 Hz

Tone burst signal:

11 cycles of a sine wave of frequency 2000 Hz. (Set to INT)

Tonio Barot org	77071	11 0,000 01 0 01110	mare of megacine, z	100	
	Ref. Level	Expected level	Tone burst signal	Tolerance	Deviation
Time wighting	dB	dB	indication(dB)	+/- dB	dB
Slow	107.0+6.6	108.0	106.9	0.5	-1.1

TIME AVERAGING TEST

This test compares the SLM reading for continuous sine signals with readings obtained from a sine tone burst sequence having the same RMS level. The test level is 30 dB below the upper limit of the linearity range and repeated for Type 1 SLM with 40 dB below the upper limit of the linearity.

Frequency of tone burst:

4000 Hz

Duration of tone burst:

1 ms

Repetition Time	Level of	Expected	Actual	Tolerance	Deviation	Remarks
	tone burst	Leq	Leq			
msec	dB	dB	dB	+/- dB	dB	
1000	85.0	85.0	84.8	1.0	-0.2	60s integ.
10000	75.0	75.0	74.6	1.0	-0.4	6min. integ



綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD.

香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533 **SMECLab**

Test Data for Sound Level Meter

Page 4 of 4

Sound level meter type:

HLES-01

Serial No.

201692136

Date

02-Apr-2019

Microphone

type:

CDM101

Serial No.

05866

Report: 19CA0329 01

PULSE RANGE AND SOUND EXPOSURE LEVEL TEST

The test tone burst signal is superimposed on a baseline signal corresponding to the lower limit of reference range

Test frequency:

4000 Hz

Integration time:

10 sec

The integrating sound level meter set to Leq:

Duration	Rms level of	Expected	Actual	Tolerance	Deviation
msec	tone burst (dB)	dB	dB	+/- dB	dB
10	103.0	73.0	72.7	1.7	-0.3

OVERLOAD INDICATION TEST

For SLM capable of operating in a non-integrating mode.

Test frequency:

2000 Hz

Amplitude:

2 dB below the upper limit of the primary indicator range.

Burst repetition frequency:

40 Hz

Tone burst signal:

11 cycles of a sine wave of frequency 2000 Hz.

Level	Level reduced by	Further reduced	Difference	Tolerance	Deviation
at overload (dB)	1 dB	3 dB	dB	dB	dB
104.1	103.1	100.1	3.0	1.0	0.0

For integrating SLM, with the instrument indicating Leq.

For integrating SLM, with the instrument indicating Leq and set to the reference range. The test signal as following: The test tone burst signal is superimposed on a baseline signal corresponding to the lower limit of reference range

Test frequency:

4000 Hz

Integration time:

10 sec

Single burst duration:

1 msec

Rms level	Level reduced by	Expected level	Actual level	Tolerance	Deviation
at overload (dB)	1 dB	dB	dB	dB	dB
109.3	108.3	68.3	68.1	2.2	-0.2

ACOUSTIC TEST

The acoustic test of the complete SLM is tested at the frequency 125 Hz and 8000 Hz using a B&K type 4226 Multifunction Acoustic Calibrator. The test is performed in A weighting.

Frequency Expected level		Actual level	Tolerar	Tolerance (dB)		
Hz	dB	Measured (dB)	+	-	dB	
1000	94.0	94.0	0.0	0.0	0.0	
125	77.9	77.7	1.0	1.0	-0.2	
8000	92.9	90.9	1.5	3.0	-2.0	

-----END-----



綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD.

香港黃竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Certificate No.:

20CA0107 02

Page:

2

Item tested

Description:

Acoustical Calibrator (Class 1)

Manufacturer: Type/Model No.: Larson Davis

Serial/Equipment No.:

13128

Adaptors used:

_

Item submitted by

Curstomer:

Lam Environmental Service Ltd.

Address of Customer:

-

Request No.: Date of receipt:

07-Jan-2020

Date of test:

08-Jan-2020

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to
Lab standard microphone	B&K 4180	2341427	03-May-2020	SCL
Preamplifier	B&K 2673	2239857	17-May-2020	CEPREI
Measuring amplifier	B&K 2610	2346941	05-Jun-2020	CEPREI
Signal generator	DS 360	33873	10-May-2020	CEPRE
Digital multi-meter	34401A	US36087050	08-May-2020	CEPREI
Audio analyzer	8903B	GB41300350	13-May-2020	CEPREI
Universal counter	53132A	MY40003662	10-May-2020	CEPREI

Ambient conditions

Temperature:

21 ± 1 °C

Relative humidity:

55 ± 10 %

Air pressure:

1000 ± 5 hPa

Test specifications

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B
 and the lab calibration procedure SMTP004-CA-156.
- 2, The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- 3, The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.

Feng Junqi

Approved Signatory:

Date:

08-Jan-2020

Company Chop:

Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

© Soils & Materials Engineering Co., Ltd

Form No.CARP156-1/Issue 1/Rev.D/01/03/2007



綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD.

黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

20CA0107 02

Page:

of

2

1. Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

			(Output level in dB re 20 μPa)
Frequency Shown Hz	Output Sound Pressure Level Setting dB	Measured Output Sound Pressure Level dB	Estimated Expanded Uncertainty
1000	94.00	93.76	0.10

Sound Pressure Level Stability - Short Term Fluctuations 2,

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz

STF = 0.009 dB

Estimated expanded uncertainty

0.005 dB

3, **Actual Output Frequency**

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz

Actual Frequency = 999.5 Hz

Estimated expanded uncertainty

0.1 Hz

Coverage factor k = 2.2

Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz

TND = 0.4 %

Estimated expanded uncertainty

0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

Date:

End

Checked by:

Date:

Shek Kwong Tai

08-Jan-2020

Fung Chi Yip 08-Jan-2020

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co., Ltd

Form No.CARP156-2/Issue 1/Rev.C/01/05/2005



Certificate of Calibration

BT-645

Particulate Monitor

Recommended calibration	n interval is	24 months	from first	day of	use.
-------------------------	---------------	-----------	------------	--------	------

Accommented Co		i vai is 24 monins ji oni ji	ist may of moci
Unit Info Model:	BT-645	81865 Firmware Rev:	1.1.0
Serial Number:	R22584	81113	0.2.4
Calibrated By:	Kevin Ricks	Cal. Date:	01/18/2019
Quality Inspector	A 25	Date:	JAN 2 1 2019
Calibration Hz/µg/m³:	9.50		
Final Test			
Flow (2.0 L/M):	Pass	Ambient T (C)	22
		RH, %	34
Serial Communication:	Pass	RH, %	34

Calibration Standards

Standards	Manufacturer	Model	SN	Cal Due
RMS Multimeter	Fluke	289 Multimeter	23740018	5/03/2019
RH &TEMPERATURE	Met One Instruments	083E-1-6	R20313	9/18/2019
Primary Flow Meter	BIOS	Defender-510	1033419	3/28/2019
Digital Dust Indicator	SIBATA	LD-3B	476795	5/18/2019

The standards used for this calibration have accuracy equal to or greater than the instrument tested. These standards are on record and traceable to NIST to the extent allowed by the institute's calibration facility. Unless otherwise stated, all instruments are calibrated to meet the manufacturer's published specifications. The Calibration system complies with MIL-STD-45662A.



Lam Environmental Services Limited

Portable Dust Meter Performance Check Record

Portable Dust Meter

Type : Particulare Monitor

Manufacturer : MET ONE INSTRUMENTS

Model Number : BT-645

Serial Number : R22584

Performance Check Date : 27-Feb-19

Standard Equipment

Type : High Volume Sampler

Manufacturer : TISCH

Model Number : TE-5170

Equipment Number : HVS018


Last Calibration Date : 4-Dec-18

Portable Dust Meter Performance Check Results


Trial no. in 1-hr period	Time	Mean Pressure (hPa)	Mean Temp (°C)	Concentration in ug/m ³ (Standard equipment) (Y - Axis)	Concentration in ug/m ³ (Performance Check / Calibrated equipment) (X - Axis)
Zero Check	27/2/19	1016	21	0	0
1	27/2/19 08:45	1016	21	75	61
2	27/2/19 09:52	1016	21	53	51
3	27/2/19 11:00	1016	21	72	58

^{*} Filter paper weighting was conducted by HOKLAS accredited laboratory.

Linear Regression of Y on X

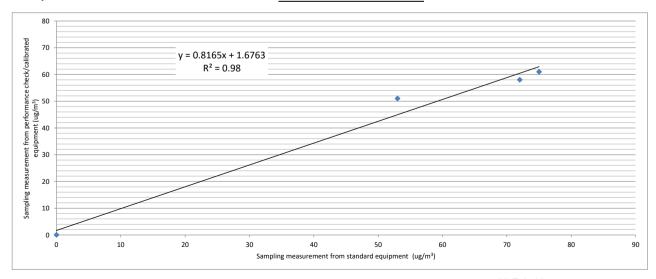

Operator:	Henry Lau	Date:	27-Feb-19	
Checked by:	Chan Ka Chun	Date:	4-Mar-19	



Certificate of Calibration

BT-645

Particulate Monitor

Recommended calibration	ı interval	is 24	months	from	first d	day e	of use.
-------------------------	------------	-------	--------	------	---------	-------	---------

Unit Info

Model:

BT-645

81865 Firmware Rev: 1.1.0

Serial Number:

R22586

81113 0.2.4

Calibrated By:

Kevin Ricks

A 21 Cal. Date: 01/18/2019

Quality Inspector:

Date: JAN 2 1 2019

Calibration Hz/μg/m³: 6.71

Final Test

Flow (2.0 L/M): Pass

Ambient T (C) ______22

RH, % 34

Serial Communication:

BT-645 Conc.: 336.53

Standard Conc:

338.79

Calibration Standards

Standards	Manufacturer	Model	SN	Cal Due
RMS Multimeter	Fluke	289 Multimeter	23740018	5/03/2019
RH &TEMPERATURE	Met One Instruments	083E-1-6	R20313	9/18/2019
Primary Flow Meter	BIOS	Defender-510	1033419	3/28/2019
Digital Dust Indicator	SIBATA	LD-3B	476795	5/18/2019

The standards used for this calibration have accuracy equal to or greater than the instrument tested. These standards are on record and traceable to NIST to the extent allowed by the institute's calibration facility. Unless otherwise stated, all instruments are calibrated to meet the manufacturer's published specifications. The Calibration system complies with MIL-STD-45662A.



Lam Environmental Services Limited

Portable Dust Meter Performance Check Record

Portable Dust Meter

Туре Particulare Monitor

Manufacturer MET ONE INSTRUMENTS

Model Number BT-645

Serial Number R22586

Performance Check Date 27-Feb-19, 14-Mar-19

Standard Equipment

Туре High Volume Sampler

Manufacturer TISCH

Model Number TE-5170

Equipment Number HVS018

Last Calibration Date 4-Feb-19


Portable Dust Meter Performance Check Results

Trial no. in 1-hr period	Time	Mean Pressure (hPa)	Mean Temp (°C)	_	Concentration in ug/m ³ (Performance Check / Calibrated equipment) (X - Axis)
Zero Check	27/2/19	1018	22	0	0
1	27/2/19 11:00	1016	24	72	58
2	27/2/19 08:45	1016	24	76	61
3	14/3/19 08:30	1018	22	104	74

^{*} Filter paper weighting was conducted by HOKLAS accredited laboratory.

Linear Regression of Y on X Slope (K- factor) Correlation Coefficient

Validity of Performance Check / Calibration Record

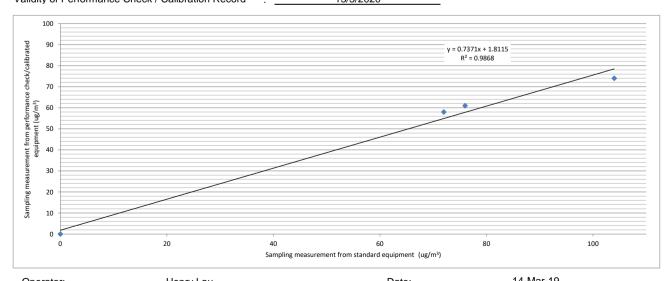

Operator:	Henry Lau	Date:	14-1/181-19
Checked by:	Chan Ka Chun	Date:	21-Mar-19
Checked by.	Chan Na Chun	Dale.	Z I-IVIAI- 13



Calibration Certificate

The calibration results on this report certify that this instrument complies with the product specifications at the time of calibration. Calibration was performed according to accepted industry methods using equipment, procedures, and standards that are traceable to NIST and ISO.

Recommended calibration interval is 12 months from the first day of use.

Instrument Model#

Aerocet 831

Instrument Serial# Y23153

%

Date of Calibration

10/30/2019

Sensor # 19493

M. Schurmann 🛕

Calibration Technician

Temperature

o_C 23

Quality Check

Relative Humidity 23

Test Procedure:

Aerocet 831-6100

PSL Size (µm)	Test Results	Test Spec.	Lot# NIST	Expiration
0.3	Pass	± 10%	196947	04/30/2021
0.5	Pass	± 10%	180556	02/28/2020
1.0	Pass	± 10%	193291	1/31/2021
2.5	Pass	± 10%	181944	3/31/2020
4.0	Pass	± 10%	REF	NA
5.0	Pass	± 10%	214115	07/31/2022
7.0	Pass	± 10%	REF	NA
10.0	Pass	± 10%	187001	07/31/2020

Standards	Model	SN	Cal Due
Particle Counter	GT-526	M1762	1/30/2020
DMM	189 Multimeter	94060816	10/2/2020
FLOWMETER	DEFENDER 510-M	172834	7/3/2020
RH/Temp Sensor	083E-1-35	R17149	8/5/2020
¥			

This calibration certificate shall not be reproduced except in full, without the written approval of Met One Instruments Inc.



Lam Environmental Services Limited

Portable Dust Meter Performance Check Record

Portable Dust Meter

Туре	: _	Particulare Monitor
	_	
Manufacturer	:	Metone AEROCET 831

Model Number : 831

Serial Number : Y23153

Performance Check Date : 3-Jan-20

Standard Equipment

Type : High Volume Sampler ____

Manufacturer : TISCH

Model Number : TE-5170

Equipment Number : HVS018

Last Calibration Date : 29-Nov-19


Portable Dust Meter Performance Check Results

				Concentration in ug/m ³	Concentration in ug/m ³
Trial no. in 1-hr period	Time	Mean Pressure (hPa)	Mean Temp (°C)	(Standard equipment)	(Performance Check / Calibrated equipment)
				(Y - Axis)	(X - Axis)
Zero Check	2/1/2019 08:00	1025	18	0	0
1	3/1/2020 09:26	1023	19	87	156
2	3/1/2020 10:27	1023	19	104	115
3	3/1/2020 11:28	1023	19	107	132

^{*} Filter paper weighting was conducted by HOKLAS accredited laboratory

Linear Regression of Y on X

Slope (K- factor) : 0.700
Correlation Coefficient : 0.918
Validity of Performance Check / Calibration Record : 2/1/20

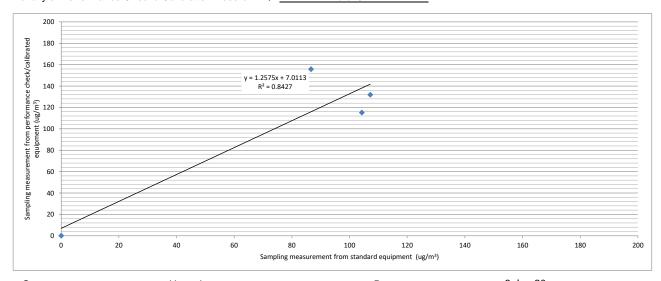

Operator:	Henry Lau	Date:	3-Jan-20	
a			4 1 00	
Checked by:	James Chu	Date:	4-Jan-20	



Certificate No.: 20190730-03

CERTIFICATE OF CALIBRATION AND TRACEABILITY

This certifies that the particle counter	HAL-HPC301 (S/N: 3011907012) for the
Customer	was produced and calibrated according to the US
Standards: ASTM F649-01 "Standard	Practice for Secondary Calibration of Airborne
Particle Counter Using Comparison P	rocedures" and ASTM F328-98 "Standard practice
for Calibration of Airborne Particle Co	ounter Using Monodisperse Spherical Particles".
The instruments and the standard part	icles used for calibrations are listed as following:

NO	Name	Туре	S/N	Calibration
1	Standard Particles	299nm±6nm	3300-022 Lot# 24932	NIST
2	Standard Particles	498nm±5nm	3500-020 Lot# 34605	NIST
3	Standard Particles	707nm±6nm	3700-018 Lot# 35148	NIST
4	Standard Particles	0.993um±0.021um	4009-022 Lot# 25628	NIST
5	Standard Particles	2.001um±0.025um	4202-024 Lot# 25754	NIST
6	Standard Particles	5.0um±0.3um	DC-05-013 Lot# 34739	NIST
7	Flowmeter	4140	41400928015	TSI
8	Oscilloscope	V-1560/100MHz	6103147	Tektronics
9	Multi-channel Signal Analyzer	MCSA-16K	4401	CITMT

Note: ASTM — American Society for Testing and Materials

NIST — National Institute of Standards and Technology

Zero Count Test: Passed

We would like to certify that all the materials, component, and workmanship used in manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by Hal Technology and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications according to required specifications and standard practice per ANSI/NCSL Z540 at the time of testing.

Test Conditions: Flow Rate 2.85 L/Min Temperature 23 °C Humidity 47 %RH

Signatory Cal Date 7-30-2019 Due Date 7-30-2020

On behalf of HAL Technology, LLC

Hal Technology, LLC, 7970 Cherry Avenue, Suite 303, Fontana, CA 92336 USA Phone/Fax: (855) GET-HALTECH or (855) 438-4258 (toll-free) Email: services@haltechnologies.com



Lam Environmental Services Limited

Portable Dust Meter Performance Check Record

Portable Dust Meter

Type : Portable Dust Meter

Manufacturer : Hal Technology

Model Number : HAL-HPC301

Serial Number : ______3011907012

Performance Check Date : 29-Aug-19

Standard Equipment

Type : High Volume Sampler

Manufacturer : TISCH

Model Number : TE-5170

Equipment Number : HVS018


Last Calibration Date : 1-Aug-19

Portable Dust Meter Performance Check Results

				Concentration in ug/m ³	Concentration in ug/m ³
Trial no. in 1-hr period	Time	Mean Pressure (hPa)	Mean Temp (°C)	(Standard equipment)	(Performance Check / Calibrated equipment)
				(Y - Axis)	(X - Axis)
Zero Check	29/8/2019 08:00	1002	29	0	0
1	29/8/2019 09:23	1002	29	30	32
2	29/8/2019 10:24	1002	29	42	26
3	29/8/2019 11:25	1002	29	33	25

^{*} Filter paper weighting was conducted by HOKLAS accredited laboratory

Linear Regression of Y on X

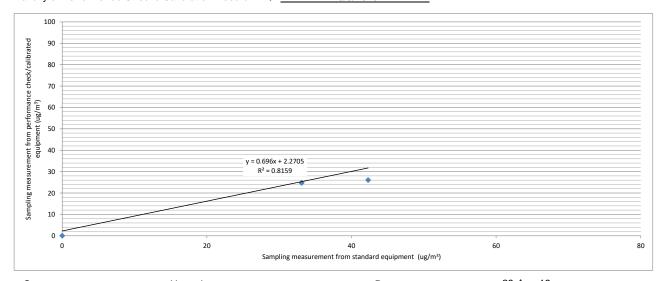

Operator:	Henry Lau	Date:	29-Aug-19	
ā			00 4 . 40	
Checked by:	James Chu	Date:	30-Aug-19	



Calibration Certificate

The calibration results on this report certify that this instrument complies with the product specifications at the time of calibration. Calibration was performed according to accepted industry methods using equipment, procedures, and standards that are traceable to NIST and ISO.

Recommended calibration interval is 12 months from the first day of use.

Instrument Model#

Aerocet 831

Instrument Serial# W15448

Date of Calibration

8/5/2019

Temperature

Sensor # 16438

Darleen Best

Calibration Technician

°C

Quality Check

Relative Humidity 43

Test Procedure:

Aerocet 831-6100

24

PSL Size (µm)	Test Results	Test Spec.	Lot# NIST	Expiration
0.3	Pass	± 10%	196947	04/30/2021
0.5	Pass	± 10%	180556	02/28/2020
1.0	Pass	± 10%	193291	1/31/2021
2.5	Pass	± 10%	181944	3/31/2020
4.0	Pass	± 10%	REF	NA
5.0	Pass	± 10%	205967	12/31/2021
7.0	Pass	± 10%	REF	NA
10.0	Pass	± 10%	187001	07/31/2020

T			
Standards	Model	SN	Cal Due
Particle Counter	GT-526	M1760	11/14/2019
Dry Cal	Defender 510	143545	12/18/2019
DMM	287	40900121	2/4/2020
RH/TEMP SENSOR	083E-1-6	R20313	9/18/2019

This calibration certificate shall not be reproduced except in full, without the written approval of Met One Instruments Inc.



Lam Environmental Services Limited

Portable Dust Meter Performance Check Record

Portable Dust Meter

Гуре	: _	Particulare Monitor

Manufacturer Metone AEROCET 831

Model Number 831

Serial Number W15448

Performance Check Date 30-Sep-19

Standard Equipment

High Volume Sampler Type

Manufacturer TISCH

Model Number TE-5170

Equipment Number HVS006


Last Calibration Date 16-Sep-19

Portable Dust Meter Performance Check Results

				Concentration in ug/m ³	Concentration in ug/m ³
Trial no. in 1-hr period	Time	Mean Pressure (hPa)	Mean Temp (°C)	(Standard equipment)	(Performance Check / Calibrated equipment)
				(Y - Axis)	(X - Axis)
Zero Check	29/9/2019 08:00	1013	29	0	0
1	30/9/2019 08:16	1009	30	149	234
2	30/9/2019 09:17	1009	30	110	145
3	30/9/2019 10:18	1009	30	167	211

Linear Regression of Y on X

Correlation Coefficient
Validity of Performance Check / Calibration Record

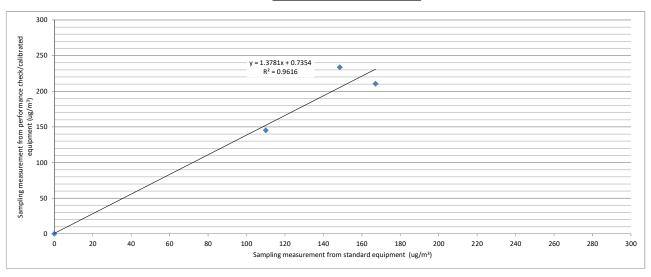

Operator:	Henry Lau	Date:	30-Sep-19
Checked by:	James Chu	Date:	1-Oct-19



Calibration Certificate

The calibration results on this report certify that this instrument complies with the product specifications at the time of calibration. Calibration was performed according to accepted industry methods using equipment, procedures, and standards that are traceable to NIST and ISO.

Recommended calibration interval is 12 months from the first day of use.

Instrument Model# Aerocet 831

Temperature

Instrument Serial# Y23154

Date of Calibration

10/30/2019

Sensor # 19494

M. Schurmann

A 14

Calibration Technician

23 °C

Quality Check

Relative Humidity 23 %

Test Procedure: Aero

Aerocet 831-6100

PSL Size (µm)	Test Results	Test Spec.	Lot# NIST	Expiration
0.3	Pass	± 10%	196947	04/30/2021
0.5	Pass	± 10%	180556	02/28/2020
1.0	Pass	± 10%	193291	1/31/2021
2.5	Pass	± 10%	181944	3/31/2020
4.0	Pass	± 10%	REF	NA
5.0	Pass	± 10%	214115	07/31/2022
7.0	Pass	± 10%	REF	NA
10.0	Pass	± 10%	187001	07/31/2020

Standards	Model	SN	Cal Due
Particle Counter	GT-526	M1762	1/30/2020
DMM	189 Multimeter	94060816	10/2/2020
FLOWMETER	DEFENDER 510-M	172834	7/3/2020
RH/Temp Sensor	083E-1-35	R17149	8/5/2020

This calibration certificate shall not be reproduced except in full, without the written approval of Met One Instruments Inc.



Lam Environmental Services Limited

Portable Dust Meter Performance Check Record

Portable Dust Meter

Гуре	:	Particulare Monitor

Manufacturer Metone AEROCET 831

Model Number

Serial Number Y23154

Performance Check Date 3-Jan-20

Standard Equipment

High Volume Sampler Type

Manufacturer TISCH

Model Number TE-5170

Equipment Number HVS018

Last Calibration Date 29-Nov-19


Portable Dust Meter Performance Check Results

Trial no. in 1-hr period	Time	Mean Pressure (hPa)	Mean Temp (°C)	Concentration in ug/m ³ (Standard equipment) (Y - Axis)	Concentration in ug/m³ (Performance Check / Calibrated equipment) (X - Axis)
Zero Check	2/1/2019 08:00	1025	18	0	0
1	3/1/2020 09:26	1023	19	87	153
2	3/1/2020 10:27	1023	19	104	112
3	3/1/2020 11:28	1023	19	107	125

Linear Regression of Y on X

Slope (K- factor)
Correlation Coefficient
Validity of Performance Check / Calibration Record

:	0.7000
:	0.9098
:	2/1/2021

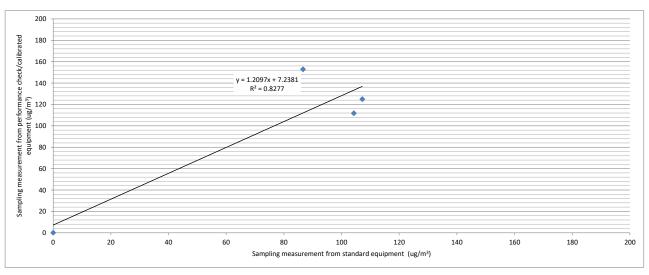


Operator:	Henry Lau	Date:	3-Jan-20
Checked by:	James Chu	Date:	4-Jan-20
Cilconoa by.	Garries erra	Date.	


Appendix 4.3


Wind data extracted from Sha Tin HKO Automatic Weather Station




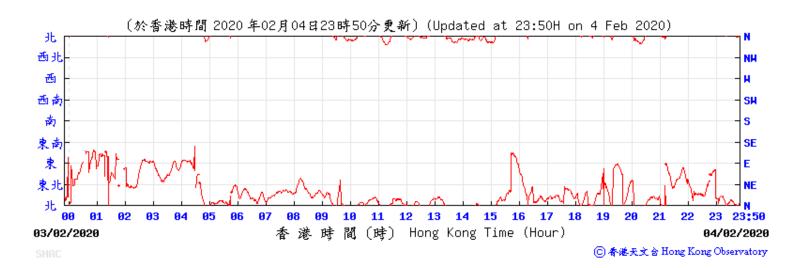




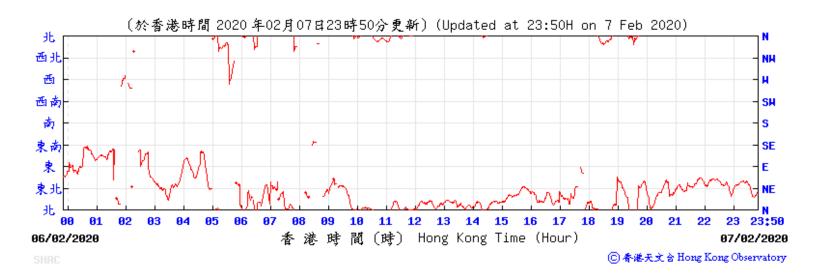


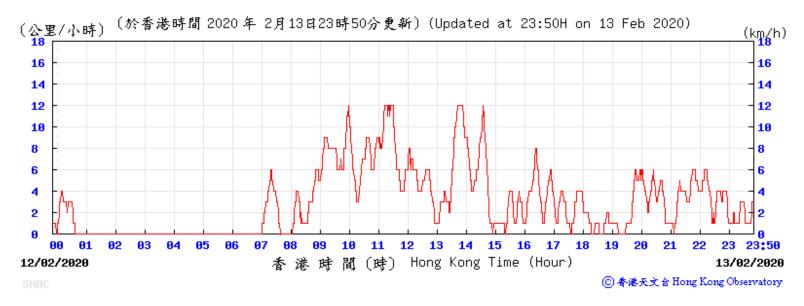


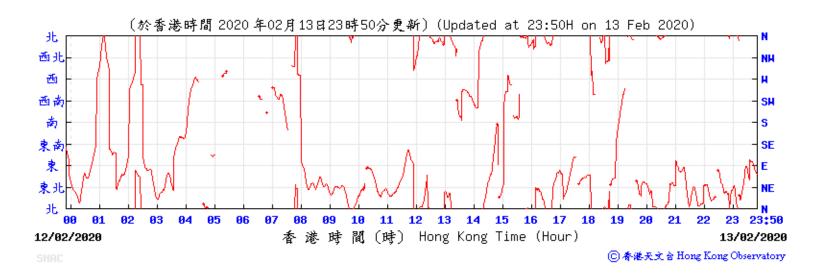



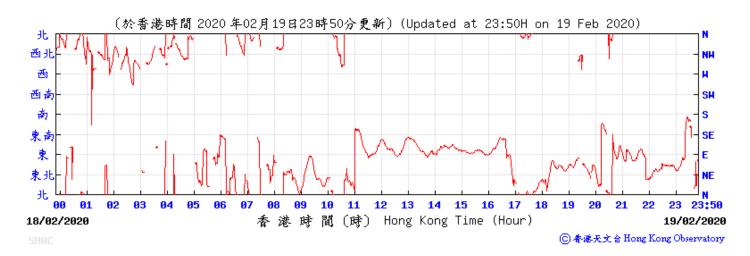

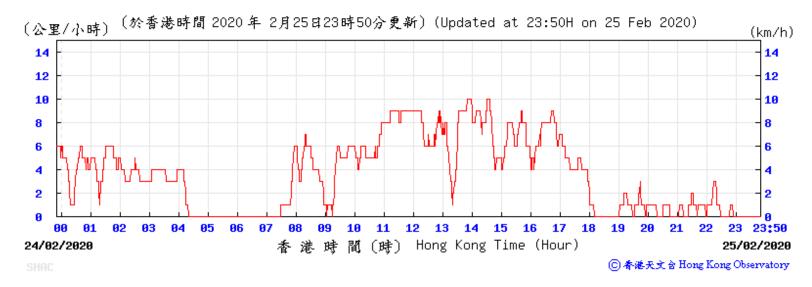

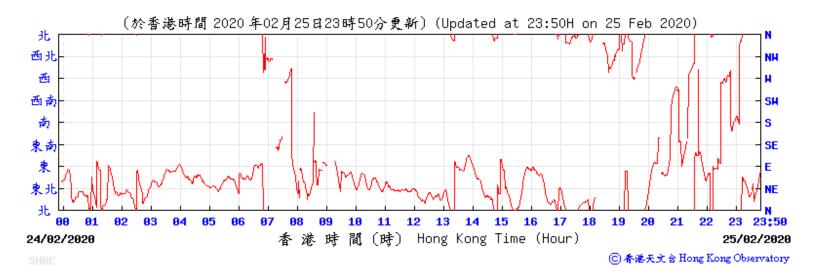

3/10/2020 Daily Extract



> Climate > Climate Information Service > Daily Extract

Daily Extract

Daily Extract of Meteorological Observations , February 2020 Back Year 2020 ▼ Month 2 ▼ King's **Hong Kong Observatory** Waglan Island[^] Park Air Temperature Mean Mean Prevailing Day Mean Total Mean Mean Dew Amount Total Absolute Absolute Relative Bright Wind Wind Pressure Mean Point of Rainfall Daily Daily Humidity Sunshine Direction Speed (hPa) Cloud (deg. (deg. (mm) Max (%) (hours) (degrees) (km/h) (%) C) C) (deg. C) (deg. C) 01 1022.4 18.8 16.0 14.1 11.0 72 29 0.0 9.1 77 *** *** 02 1022.0 19.5 17.1 15.9 13.1 85 0.0 1.6 *** 03 1020.3 20.4 18.1 16.6 14.1 78 68 Trace 1.9 *** *** 04 1020.2 19.0 17.3 15.4 14.5 84 88 0.8 0.6 *** *** 05 1020.6 18.3 17.5 16.6 14.7 83 88 1.0 0.2 06 1019.8 18.6 17.1 15.9 13.1 77 81 Trace 1.5 *** 07 1021.1 20.6 18.7 17.3 15.4 82 85 0.0 0.5 80 1024.0 19.6 17.8 16.7 13.5 76 88 0.0 0.1 *** *** *** 09 1025.7 18.5 16.5 15.0 12.4 77 88 Trace 0.1 *** 10 1023.1 18.6 16.9 15.5 12.7 76 88 0.0 0.3 11 1020.5 19.1 17.6 16.8 15.2 86 88 8.0 0.0 *** 12 1017.9 24.7 20.6 18.4 18.6 89 77 0.0 4.9 *** *** 1015.4 13 19.6 18.7 80 0.3 20.5 18.9 94 41.6 14 1013.8 22.5 20.4 19.5 19.5 94 92 9.7 1.7 *** *** 15 1013.6 22.3 21.0 19.4 20.0 95 92 Trace 8.0 *** 1020.1 22.4 14.2 10.6 11.0 82 92 0.9 16 25.5 17 1026.2 18.0 13.6 10.3 4.0 53 26 10.3 *** *** 0.0 18 1026.4 18.4 14.7 11.6 6.1 57 6 0.0 10.5 *** *** 1024.6 19 19.4 16.3 14.0 10.4 69 37 0.0 7.6 *** 20 1024.9 21.2 17.7 15.4 12.0 70 31 0.0 6.7 *** 7 21 1026.7 22.6 18.9 16.5 14.0 73 0.0 10.6 *** 22 1025.7 25.5 20.1 17.1 15.0 73 11 0.0 10.5 *** 23 1024.6 23.9 19.4 17.5 14.0 71 67 0.0 6.7

22.0

19.6

15.3

76

0.0

1.5

1020.7

3/10/2020 Daily Extract

25	1017.9	25.0	21.8	19.7	19.0	84	56	Trace	3.6	***	***
26	1017.9	28.1	23.3	20.6	19.9	82	29	0.0	10.4	***	***
27	1019.6	22.6	20.5	19.1	17.6	84	78	0.4	4.1	***	***
28	1018.0	25.3	20.8	18.1	16.7	78	84	0.0	5.5	***	***
29	1014.7	26.6	22.5	20.2	18.8	80	54	0.0	5.7	***	***
Mean/Total	1021.0	21.4	18.5	16.6	14.5	78	65	79.8	118.2	***	***
Normal?	1018.5	18.9	16.8	15.0	13.0	80	74	54.4	94.2	070	24.5

^{***} unavailable

^{? 1981-2010} Climatological Normal, unless otherwise specified



[^] Information of wind direction and wind speed for Waglan Island are based on automatic weather station data since January 1989

Trace means rainfall less than 0.05 mm

Appendix 5.1

Monitoring Schedules for Reporting Month and Next Month



Contract No. SPW 25/2018

Environmental Team for Relocation of Sha Tin Sewage Treatment Works to Caverns –Site Preparation and Access Tunnel Construction Tentative Impact Air Quality and Noise Monitoring Schedule February 2020

February 2020								
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday		
26-Jan	27-Jan	28-Jan	29-Jan	30-Jan	31-Jan	1-Feb		
			AQM (AM1, AM2, AM4, AM5)					
			NM (CM1, CM3, CM4, CM5)					
2-Feb	3-Feb	4-Feb	5-Feb	6-Feb	7-Feb	8-Feb		
Z-Feb	3-Feb		5-Feb	6-FeD		8-Feb		
		AQM (AM1, AM2, AM4, AM5)			AQM (AM1, AM2, AM4, AM5)			
		NM (CM1, CM3, CM4, CM5)						
9-Feb	10-Feb	11-Feb	12-Feb	13-Feb	14-Feb	15-Feb		
				AQM (AM1, AM2, AM4, AM5)				
				NM (CM1, CM3, CM4, CM5)				
				(0, 0, 0, 0,				
16-Feb	17-Feb	18-Feb		20-Feb	21-Feb	22-Feb		
			AQM (AM1, AM2, AM4, AM5)					
		NM (CM1, CM4)	NM (CM3, CM5)					
23-Feb	24-Feb	25-Feb	26-Feb	27-Feb	28-Feb	29-Feb		
		AQM (AM1, AM2, AM4, AM5)						
		NM (CM1, CM3, CM4, CM5)						
		(0, 0, 0, 0)						
Remark:								

Remark:

- 1. AQM: Air Quality Monitoring
 - NM: Noise Monitoring, the monitoring date may be changed depends on whether and arrangement
- 2. Air quality and noise monitoring were suspended due to site closed with no scheduled site activities from 29 January to 2 February 2020



Contract No. SPW 25/2018

Environmental Team for Relocation of Sha Tin Sewage Treatment Works to Caverns –Site Preparation and Access Tunnel Construction Tentative Impact Air Quality and Noise Monitoring Schedule March 2020

r	March 2020									
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday				
1-Mar	2-Mar	3-Mar	4-Mar	5-Mar	6-Mar	7-Mar				
	AQM (AM1, AM2, AM4, AM5)					AQM (AM1, AM2, AM4, AM5)				
	NM (CM1, CM3, CM4, CM5)									
8-Mar	9-Mar	10-Mar	11-Mar	12-Mar	13-Mar	14-Mar				
					AQM (AM1, AM2, AM4, AM5) NM (CM1, CM3, CM4, CM5)					
15-Mar	16-Mar	17-Mar	18-Mar	19-Mar	20-Mar	21-Mar				
				AQM (AM1, AM2, AM4, AM5) NM (CM1, CM3, CM4, CM5)						
22-Mar	23-Mar	24-Mar	25-Mar AQM (AM1, AM2, AM4, AM5) NM (CM1, CM3, CM4, CM5)	26-Mar	27-Mar	28-Mar				
29-Mar	30-Mar	31-Mar AQM (AM1, AM2, AM4, AM5) NM (CM1, CM3, CM4, CM5)	1-Apr	2-Apr	3-Apr	4-Apr				

1. AQM: Air Quality Monitoring

NM: Noise Monitoring, the monitoring dates are tentative and are subject to change

Appendix 5.2

Air Quality Monitoring Results and Graphical Presentations



Report on 1-hour TSP monitoring at AM1 - Ah Kung Kok Fishermen Village

294 Action Level (µg/m3) -Limit Level (µg/m3) -500

Date	Weather Condition	Time	Mass Concentration (µg/m3)
4-Feb-20	Fine	08:35	17
4-Feb-20	Fine	09:36	14
4-Feb-20	Fine	10:37	19
7-Feb-20	Fine	08:38	82
7-Feb-20	Fine	09:39	83
7-Feb-20	Fine	10:40	81
13-Feb-20	Fine	08:26	82
13-Feb-20	Fine	09:27	81
13-Feb-20	Fine	10:28	67
19-Feb-20	Fine	09:37	21
19-Feb-20	Fine	10:38	19
19-Feb-20	Fine	13:02	13
25-Feb-20	Fine	08:39	169
25-Feb-20	Fine	09:40	161
25-Feb-20	Fine	10:41	138



Report on 1-hour TSP monitoring at AM2 - Block H, Kam Tai Court

325 Action Level (µg/m3) -500 Limit Level (µg/m3) -

Date	Weather Condition	Time	Mass Concentration (µg/m3)
4-Feb-20	Fine	09:19	27
4-Feb-20	Fine	10:20	25
4-Feb-20	Fine	13:00	36
7-Feb-20	Fine	08:58	25
7-Feb-20	Fine	09:59	29
7-Feb-20	Fine	11:00	31
13-Feb-20	Fine	09:23	94
13-Feb-20	Fine	10:24	88
13-Feb-20	Fine	13:00	31
19-Feb-20	Fine	10:13	85
19-Feb-20	Fine	13:01	52
19-Feb-20	Fine	14:02	46
25-Feb-20	Fine	08:56	191
25-Feb-20	Fine	09:57	208
25-Feb-20	Fine	10:58	220



Report on 1-hour TSP monitoring at AM4 - Wellborn Kindergarten

Action Level (μ g/m3) - 297 Limit Level (μ g/m3) - 500

Date	Weather Condition	Time	Mass Concentration (µg/m3)
4-Feb-20	Fine	09:01	25
4-Feb-20	Fine	10:01	25
4-Feb-20	Fine	13:00	32
7-Feb-20	Fine	08:34	60
7-Feb-20	Fine	09:35	59
7-Feb-20	Fine	10:36	60
13-Feb-20	Fine	08:22	64
13-Feb-20	Fine	09:23	44
13-Feb-20	Fine	10:24	46
19-Feb-20	Fine	13:00	40
19-Feb-20	Fine	14:01	37
19-Feb-20	Fine	15:02	55
25-Feb-20	Fine	08:32	168
25-Feb-20	Fine	09:33	163
25-Feb-20	Fine	10:34	150




Report on 1-hour TSP monitoring at AM5 - The NAAC Harmony Manor


Action Level (μ g/m3) - 349 Limit Level (μ g/m3) - 500

Date	Weather Condition	Time	Mass Concentration (µg/m3)
4-Feb-20	Fine	09:58	35
4-Feb-20	Fine	10:59	29
4-Feb-20	Fine	13:00	40
7-Feb-20	Fine	08:07	38
7-Feb-20	Fine	09:08	37
7-Feb-20	Fine	10:09	33
13-Feb-20	Fine	08:52	57
13-Feb-20	Fine	09:53	63
13-Feb-20	Fine	10:54	62
19-Feb-20	Fine	11:00	25
19-Feb-20	Fine	13:01	20
19-Feb-20	Fine	14:02	19
25-Feb-20	Fine	08:43	209
25-Feb-20	Fine	09:44	202
25-Feb-20	Fine	10:45	202




Graphic Presentation of TSP Result

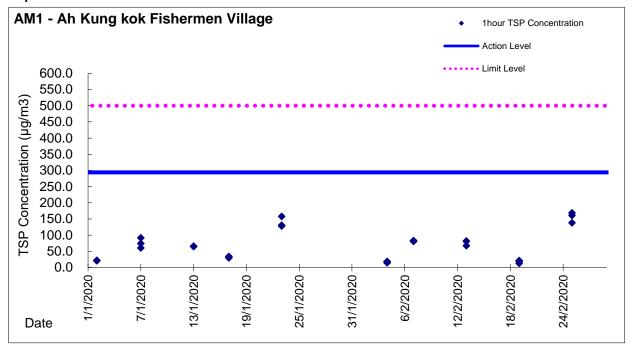


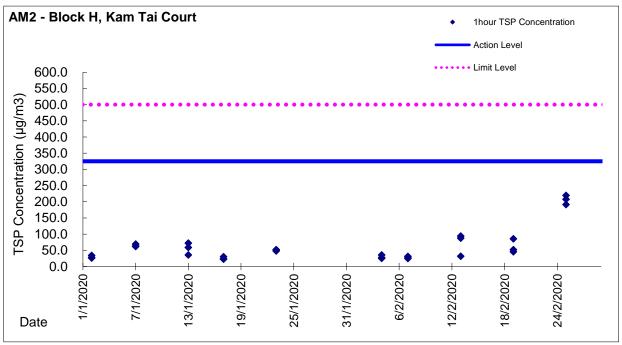



Graphic Presentation of TSP Result

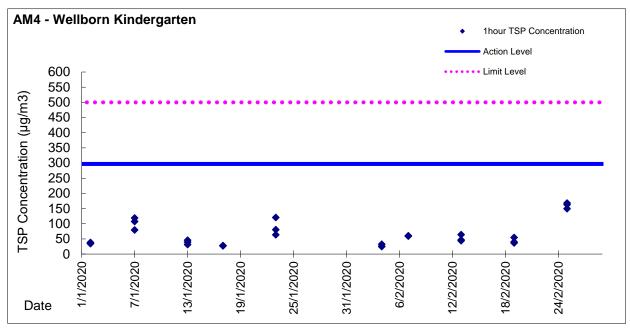

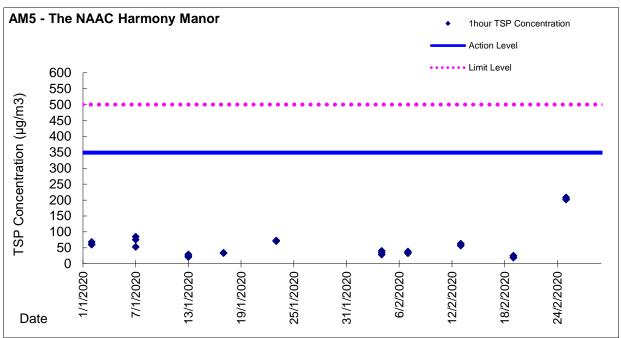

Appendix 5.3

Noise Quality Monitoring Results and Graphical Presentations



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: CM1 - G/F, Wellborn Kindergarten

				Measurement Noise Level Limit Level				
Date	Time	Weather	Wind Speed	Leq	L10	L90	Leq	
			(m/s)		Unit	:: dB(A), (3	30min)	
04/02/2020	14:00	Cloudy	0.0	52.6	55.0	49.5	70	
13/02/2020	9:00	Cloudy	0.0	53.4	56.5	48.5	70	
18/02/2020	8:40	Fine	0.0	57.6	59.0	56.0	70	
25/02/2020	10:40	Cloudy	0.0	56.7	60.0	50.0	70	

^{*} Limit level of noise monitoring station CM1 was adjusted to 65dB(A) during examination period.

Location: CM3 - R/F, S.K.H. Ma On Shan Holy Spirit Primary School

				Measurement Noise Level Limit Level			
Date	Time	Weather	Wind Speed	Leq	L10	L90	Leq
			(m/s)		Unit	:: dB(A), (3	30min)
04/02/2020	11:15	Cloudy	0.1	63.3	65.0	60.5	70
13/02/2020	09:45	Cloudy	0.5	62.5	66.0	59.5	70
19/02/2020	10:40	Fine	0.3	62.6	64.0	60.0	70
25/02/2020	10:00	Cloudy	0.0	64.3	67.5	59.5	70

^{*} Limit level of noise monitoring station CM3 was adjusted to 65dB(A) during examination period.

Location: CM4 - G/F, Ah Kung Kok Fishermen Village

				Measurement Noise Level Limit Leve				
Date	Time	Weather	Wind Speed	Leq	L10	L90	Leq	
			(m/s)		Unit	:: dB(A), (3	30min)	
04/02/2020	14:39	Cloudy	0.0	62.1	63.5	57.9	75	
13/02/2020	10:20	Cloudy	0.0	63.8	66.5	58.0	75	
18/02/2020	9:20	Fine	0.0	66.9	69.5	62.5	75	
25/02/2020	13:40	Cloudy	0.0	63.6	67.5	59.0	75	

Location: CM5 - R/F, The Neighbourhood Advice-Action Council Harmony Manor

				Measurement Noise Level Limit Level				
Date	Time	Weather	Wind Speed	Leq	L10	L90	Leq	
			(m/s)		30min)			
04/02/2020	09:55	Cloudy	0.2	59.2	61.0	54.0	75	
13/02/2020	11:10	Cloudy	0.0	60.6	63.5	55.0	75	
19/02/2020	11:30	Fine	0.8	54.1	58.5	49.5	75	
25/02/2020	13:00	Cloudy	0.0	55.8	57.5	51.0	75	


^{*} Free field correction (Additional 3dB(A)) was made on CM1&CM4 measurement result





Environmental Team for Relocation of Sha Tin Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

Graphic Presentation of Noise Monitoring Result












Environmental Team for Relocation of Sha Tin Sewage Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

Graphic Presentation of Noise Monitoring Result Day Time (0700 - 1900hrs on normal weekdays)



Appendix 5.4

Monthly Summary Waste Flow Table

Monthly Summary Waste Flow Table

Contract No.: DC/2018/05

Name of Department: <u>Drainage Services Department</u>

Monthly Summary Waste Flow Table for February 2020 [to be submitted not later than the 15th day of each month following reporting month]

(All quantities shall be rounded off to 3 decimal places.)

(All qualit	tities shall be round	ieu on to 3 decima	i piaces.)							
	Ac	tual Quantities of I	nert C&D Materia	ls Generated Mont	hly		Actual Quantities	of C&D Wastes C	Generated Monthly	
	(a)=(b)+(c)+(d)+(e)	(b)	(c)	(d)	(e)	(f)	(g)	(h)	(i)	(j)
Month	Total Quantity	Broken Concrete	Reused in the	Reused in other	Disposed as	Metals	Paper/cardboard	Plastics		Others, e.g. general
	Generated	(see Note 3)	Contract	Projects	Public Fill		packaging	(see Note 2)	Chemical Waste	refuse disposed at
										Landfill
	(in '000m ³)	(in '000kg)	(in '000kg)	(in '000kg)	(in L)	(in tonne)				
Jan-20	0.000	0.000	0.063	5.297	0.011	0.000	0.000	0.000	0.0	19.72
Feb-20	14.478	0.038	0.000	14.049	0.391	0.000	0.000	0.000	320	78.23
Sub-total	14.478	0.038	0.063	19.346	0.402	0.000	0.000	0.000	320.000	97.95
Total	14.478	0.038	0.063	19.346	0.402	0.000	0.000	0.000	320.000	97.95

Notes:

- (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (2) Plastics refer to plastics bottles/containers, plastic sheets/foam from packaging material.
- (3) Broken concrete for recycling into aggregates.
- (4) If necessary, use the conversion factor: 1 full load of 24T, 30T & 38T dumping truck is equivalent to 5 m³, 7m³, & 10.5m³ by volume respectiverly.
- (5) Conversion factors for reporting purpose:

Excavated: $rock = 2.0 \text{ tonnes/m}^3$, $soil = 1.8 \text{ tonnes/m}^3$, broken concrete and bitumen = 2.4 tonnes/m³, Slurry = 2.8 tonnes/m³

Appendix 6.1

Event Action Plans

Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin Sewage
Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

Event and Action Plan for Construction Air Quality

EVENT		ACTION		
EVENI	ET	IEC	ER	CONTRACTOR
ACTION LEVEL				
Action level being exceedance by one sampling	Identify source, investigate the causes of exceedance and propose remedial measures; Inform Contractor, IEC and ER; Repeat measurement to confirm finding; and Increase monitoring frequency to daily.	Check monitoring data submitted by ET; Check Contractor's working method; and Review and advise the ET and ER on the effectiveness of the proposed remedial measures.	1. Notify Contractor.	Identify source(s), investigate the causes of exceedance and propose remedial measures; Implement remedial measures; and Amend working methods agreed with the ER as appropriate
2. Action level being exceeded by two or more consecutive sampling	 Identify source; Inform Contractor, IEC and ER; Advise the Contractor and ER on the effectiveness of the proposed remedial measures; Repeat measurements to confirm findings; Increase monitoring frequency to daily; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with Contractor, IEC and ER; If exceedance stops, cease additional monitoring. 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET, ER and Contractor on possible remedial measures; Advise the ET and ER on the effectiveness of the proposed remedial measures; and Supervise Implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Notify Contractor; Ensure remedial measures properly implemented. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Identify source and investigate the causes of exceedance; Submit proposals for remedial measures to the ER with a copy to ET and IEC within three working days of notification; Implement the agreed proposals; and Amend proposal as appropriate.



Event and Action Plan for Construction Air Quality (Con't)

EVENT				
EVENI	ET	IEC	ER	CONTRACTOR
LIMIT LEVEL				
1. Limit level exceedance by one sampling	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform Contractor, IEC, ER, and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; and Assess effectiveness of Contractor's remedial actions and keep IEC, EPE and ER informed of the results. 		Confirm receipt of notification of exceedance in writing; Notify Contractor; Ensure remedial measures properly implemented.	Identify source(s) and investigate the causes of exceedance; Take immediate action to avoid further exceedance; Submit proposals for remedial measures to ER with a copy to ET and IEC within three working days of notification; Implement the agreed proposals; and Amend proposal if appropriate.
2. Limit level exceedance by two or more consecutive sampling	 Notify IEC, ER, Contractor and EPD 2. Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and If exceedance stops, cease additional monitoring. 	by the ET; 2. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 3. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 4. Supervise the implementation of remedial measures.	 Confirm receipt of notification of exceedance in writing; In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures; and If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Identify source(s) and investigate the causes of exceedance; Take immediate action to avoid further exceedance; Submit proposals for remedial measures to the ER with a copy to the IEC and ET within three working days of notification; Implement the agreed proposals; Revise and resubmit proposals if problem still not under control; and Stop the relevant portion of works as determined by the ER until the exceedance is abated.



Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin Sewage
Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

Event and Action Plan for Construction Noise

EVENT	ACTION													
	ET	IEC	ER	CONTRACTOR										
Action Level	Notify IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, ER and Contractor; Discuss with the Contractor and formulate remedial measures; and Increase monitoring frequency to check mitigation effectiveness.	Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the ER accordingly; and Supervise the implementation of remedial measures	 Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analyzed noise problem; and Ensure remedial measures are properly implemented. 	Submit noise mitigation proposals to IEC; and Implement noise mitigation proposals.										
Limit Level	 Identify source; Inform IEC, ER, EPD and Contractor; Repeat measurements to confirm findings; Increase monitoring frequency; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Inform IEC, ER and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. 	Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and Supervise the implementation of remedial measures.	 Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; and If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC and ER within 3 working days of notification; Implement the agreed proposals; Resubmit proposal if problem still not under control; and Stop the relevant portion of works as determined by the ER until the exceedance is abated. 										

Appendix 6.2

Summary for Notification of Exceedance



Contract No. SPW 25/2018 Lam Environmental Services Limited Environmental Team for Relocation of Sha Tin Sewage Treatment Works to Caverns – Site Preparation and Access Tunnel Construction

Ref no.	Date	Location	Parameters (Unit)	Measured	Action Level	Limit Level	Follow-up action
-	-	-	-	-	-	-	-

Appendix 8.1

Complaint Log



Contract No. SPW 25/2018
Environmental Team for Relocation of Sha Tin Sewage
Treatment Works to Caverns –
Site Preparation and Access Tunnel Construction

Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					A public complaint regarding construction dust received by DSD on 29 July 2019 was subsequently referred to ET on 6 August 2019. The complainant reported that exposed slope surface without any covering at Portion 6. Based on the information provided by the Contractor, the concerned area was under slope cutting and filling works for temporary haul road construction.	
					Based on the observation on 6 August 2019 and weekly site inspection on 7 August 2019, the concerned slope was observed covered with the tarpaulin sheets to alleviate the potential dust impact to the surroundings.	Interim investigatio
190808	29 July 2019	DSD	Construction site area Portion 6	Exposed slope surface without any covering was observed at Portion 6	Upon review on the monitoring data, no exceedances were recorded at the air quality monitoring stations AM2 - Block H, Kam Tai Court and AM4 - Wellborn Kindergarten (located nearest to the concerned slope) during the 1hr TSP monitoring on 23 July 2019 and 29 July 2019 respectively.	n report was issue on 16 August 2019
				Follow up site inspection was conducted by the Environmental Team on 07 August 2019 and it was observed that the slope at Portion 6 was properly covered.		
					Nevertheless, in view of the public concern, the Contractor of DC/2018/05 was reminded to enhance the dust suppression measure by providing adequate watering to any exposed surface during cutting slope and fill works to avoid potential dust impact to the surroundings.	

Appendix 9.1

Construction Programme of Individual Contracts

Relocation of Sha Tin	Sewage Treatment Works to Caverns (8-Jan-20)		_		3 Moi	nth Rolling Pr	rogramme					Page	e 1 of 8
ctivity ID	Activity Name	Original Duration	Start	Finish	Total Float	Late Start	Late Finish	2019			2020		
Polocation of S	Sha Tin Sewage Treatment Works to Ca	avorne Sito Pron	ration & A	Accoss Tunno				Dec	Jan	Feb	Mar	Apr	May
Preliminary Wo		avems - Site Piepa	iration & F	iccess fulfile									-
Preliminary Works										1 1 1			
Preliminary Wo										1			
A11980	Preservation and Protection of Existing Trees	836	28-Feb-19 A	28-Dec-21	0	28-Dec-21	28-Dec-21						
A12340	Establishment Works to landscape softworks (Section 7)	719	23-Jul-19A	28-Dec-21	0	23-Jul-19	28-Dec-21						
Across Road t	o Main Portal Area												-
Tree Treatment	o Maiii i Ottai Area												-
Tree Treatment										1			+
A11032	Tree transplant (Portion 4)	82	09-Sep-19A	15-Jan-20	103	21-May-20	28-May-20						
A15290	Tree felling & protection (Mui Tsz Lam Road realigment)	27	08-Nov-19 A	08-Jan-20	513	08-Oct-21	08-Oct-21						
A15300	Tree transplant (Mui Tsz La m Road re ali gment)	95	01-Nov-19 A	27-Mar-20	451	26-Jul-21	08-Oct-21						
Steel Bridge										1			
North Tower of	Steel Bridge									1			
A10293	Abutment (North Ramp)	26	29-Feb-20	30-Mar-20	10	12-Mar-20	15-Apr-20			-			
A10295	North Ramp (GL13-16/A1-C) fabrication complete & ready to delivery	y on site 0	28-Mar-20*		12	16-Apr-20					1	orth Ramp (GL13-16/A1-C)fabri	ication con
A10296	North Ramp (GL11-13/A1-C) fabrication complete & ready to delivery	y on site 0	17-Mar-20*		28	23-Apr-20				-	◆ North Ramp (GL11-13/A1-C) fabrication comp	lete & read
A10297	North Tower fabrication complete & ready to delivery on site	0	08-Feb-20*		10	20-Feb-20				North Tower fabrication	n complete & ready to delivery on s	ite	
A10300	Steel Piers & deck erection (North Tower)	13	08-Feb-20	22-Feb-20	10	20-Feb-20	05-Mar-20						
A10303	North Ramp (GL11-13/A1-C) steel work installation	12	17-Mar-20	30-Mar-20	28	23-Apr-20	08-May-20						
A10304	North Ramp (GL13-16/A1-C) steel work installation	12	31-Mar-20	17-Apr-20	10	16-Apr-20	29-Apr-20						
		12	314VIAI-20	17-740-20	10	10740120	29401-20			1			-
South Tower of A10340	Steel Bridge Abutment (South Ramp)	36	03-Jan-20 A	20-Feb-20	26	14-Feb-20	21 - Mar-20						
A10345	Steel Piers & deck (South Tower & Ramp) fabrication complete & rea		28-Feb-20*	2010020	20	23-Mar-20	Z i Wai Zo				Steel Diem 9 deek/South Tours	Down) foliantian as mulate 9	maduta da
	site			44.0400			00.400				Steel Piers & deck (South Tower &	Ramp) labilication complete & r	eady to de
A10350	Steel Piers & deck erection (South Tower & Ramp)	14	28-Feb-20	14-Mar-20	20	23-Mar-20	08-Apr-20						
A10356	Concreting slab for South Ramp	6	16-Mar-20	21-Mar-20	20	09-Apr-20	18-Apr-20						
A10360	Barrier	12	23-Mar-20	06-Apr-20	20	20-Apr-20	05-May-20						
Main Span					,								
A10371	Temp Tower for Main Span erection	13	03-Feb-20*	17-Feb-20	15	20-Feb-20	05-Mar-20						
A10372	Main Span (North Side) steel work fabrication complete & ready to de	delivery on site 0	08-Feb-20*		604	26-Feb-22				◆ Main Span (North Sid	e)steel work fabrication complete &	ready to delivery on site	
A10373	Main Span (South Side) steel work fabrication complete & ready to d	delivery on site 0	16-Mar-20*		37	05-May-20					♦ Main Span (So	uth Side)steel work fabrication	complete {
A10375	Main Span (North Side) steel work installation	5	24-Feb-20	28-Feb-20	10	06-Mar-20	11-Mar-20						
A10377	Main Span (South Side) steel work installation	5	16-Mar-20	20-Mar-20	37	05-May-20	09-May-20						
A10378	Welding & Testing (Main span)	10	21-Mar-20	01-Apr-20	37	11-May-20	21-May-20)	
A10390	Concreting slab for Main Span	6	02-Apr-20	09-Apr-20	37	22-May-20	28-May-20			- L			
Noise Barrier		l l											
Design													
A15020	Noise Barrier Design approval (NB1 & NB3)	158	09-Jul-19 A	13-Jan-20	656	24-Oct-21	29-Oct-21						
NB1		'		·									
Remaining Level of						Contract	t No. DC/20	18/05					
Actual Level of Effor		e		Relocation				ent Works to C	averns -		III	0.74.75	
Remaining Work	Data Date: 08-Jan-20 Page 1 of 8						_	nnel Construct				STATE	
Critical Remaining	_	s, Inc.					olling Prog			L	JOINT \	/ENTURE	
Milestone♦ Crit. Milestone					_		5 - 5						
													ļ

Relocation of Sha T	Fin Sewage Treatment Works to Caverns (8-Jan-20)				3 Mc	onth Rolling Pro	ogramme					F	Page 2 of 8
activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Late Start	Late Finish	2019			2020		
A10800	NB post installation - NB1 (0-75m)	13	08-Jan-20	22-Jan-20	548	19-Nov-21	03-Dec-21	Dec	Jan	Feb	Mar	Apr	May
	<u> </u>								· <u></u>	<u> </u>			
A10810	NB panel installation - NB1 (0-75m)	13	23-Jan-20	13-Feb-20	548	04-Dec-21	18-Dec-21						
A10850	NB post installation - NB1 (75-150m)	13	23-Jan-20	13-Feb-20	548	04-Dec-21	18-Dec-21					 	
A10860	NB panel installation - NB1 (75-150m)	7	14-Feb-20	21-Feb-20	548	20-Dec-21	29-Dec-21						
NB2										1		1 1 1	
A10910	NB frame installation - NB2 (0-63m)	13	31-Mar-20	18-Apr-20	496	04-Dec-21	18-Dec-21					!	
NB3												1	
A10940	Excavation - NB3 (0-25m)	6	13-Jan-20	20-Jan-20	527	30-Oct-21	05-Nov-21						
A10950	Footing & wall structure - NB3 (0-25m)	25	20-Jan-20	25-Feb-20	527	06-Nov-21	04-Dec-21						
A10960	Backfill -NB3 (0-25m)	7	25-Feb-20	04-Mar-20	527	06-Dec-21	13-Dec-21						
A10970	NB post installation - NB3 (0-25m)	6	04-Mar-20	11-Mar-20	527	14-Dec-21	20-Dec-21			-			
A10980	NB panel installation - NB3 (0-25m)	6	11-Mar-20	18-Mar-20	527	21-Dec-21	29-Dec-21			-	 		
	<u> </u>	0	11-Ivial-20	10-IVIAI-20	521	21-060-21	29-Dec-21			 		 	
Water Mains D										1		1 1 1	
DN600 Water		26	29 Dec 10 A	15 Fab 20	202	07 Ion 21	00 Feb 21						
A10550	Jacking pit at CHA 80.2 (Portion 4)	36	28-Dec-19 A	15-Feb-20	293	07-Jan-21	08-Feb-21			i 		: 	
A10560	Jacking pit at CHA 115.1 (Portion 6)	36	17-Feb-20	28-Mar-20	293	09-Feb-21	29-Mar-21						
DN450 Water	r Main									!		 	
A10660	ELS (CHB 0 - 37)	15	08-Jan-20	24-Jan-20	307	23-Jan-21	09-Feb-21			1		1 1 1	
A10670	Excavation (CHB 0 -37)	21	01-Feb-20	25-Feb-20	307	10-Feb-21	12-Mar-21						
A10680	Laying DN450 (CHB 0 -37)	60	26-Feb-20	12-May-20	307	13-Mar-21	27-May-21			-			
Drainage Worl	ks									i 		i 1 1	
	Road Realigment									 		1	
A10400	TTA submission & approval	37	13-Nov-19 A	24-Jan-20	31	20-Feb-20	07-Mar-20						
A10995	Drainage work from SMH2010 to 2011 (2mh ~6 to 7.5m depth)	90	01-Feb-20	22-May-20	179	07-Sep-20	23-Dec-20						
A13230	Jacking pit in portion 6 for 1350 dia pipe jacking	28	05-Feb-20	07-Mar-20	28	09-Mar-20	14-Apr-20			-			
A13240	Jacking pit in portion 4 for 1350 dia pipe jacking	46	06-Nov-19 A	04-Feb-20	28	17-Feb-20	07-Mar-20			-		 	
											<u></u>		
A13250	Pipe Jacking for 1350 dia drainage (60m)	80	09-Mar-20	16-Jun-20	28	15-Apr-20	21-Jul-20					1	- !
Road Works												1	
	ditional RW along Cycle Track and Footpath in Portion 1		lana and	1		1	1						
A16960	Pavement work	5	08-Jan-20	13-Jan-20	35	25-Feb-20	29-Feb-20						
A16970	Railing installation	6	09-Jan-20	15-Jan-20	35	26-Feb-20	03-Mar-20					1	
Haul Road U	nder Ma On Shan Rail											1	
A11900	Existing Cycle track and footpath diversion	2	16-Jan-20	17-Jan-20	35	04-Mar-20	05-Mar-20						
A11938	Haul Road Design approval	21	08-Jan-20	28-Jan-20	37	14-Feb-20	05-Mar-20			- 		-	
A11940	Haul Road Construction	66	01-Feb-20	22-Apr-20	29	06-Mar-20	28-May-20						
Construction	n Access connecting Ma On Shan Road									1		1	
A13340	Construction Access Connecting Ma On Shan Road construction at Portion 4	18	08-Jan-20	04-Feb-20	92	08-May-20	28-May-20						
A13420	Construction Access Connecting Ma On Shan Road construction at Portion 2	52	18-Feb-20	22-Apr-20	29	23-Mar-20	28-May-20						
A13870	Access connecting Tunnel Acces to Steel Bridge Construction Access Connecting Tunnel Access to Steel Bridge	20	07-Apr-20	05-May-20	20	06-May-20	28-May-20						
		20	07 73p120	55 Way-20	20	00 May-20	201VIQY*20			<u> </u>			
Main Portal										1 1 1		: 	
Site Formation										1 1 1		1 1 1	
Slope SMP 2		47	00 los 00	02 Fab 00	202	12 0-4 20	00 Nov 00						
A12800	Soil Nail at 30.0mpd (Ae1-67)-67nos	17	08-Jan-20	03-Feb-20	223	13-Oct-20	02-Nov-20						

Relocation of Sha	Tin Sewage Treatment Works to Caverns (8-Jan-20)				3 Mo	nth Rolling Pr	ogramme				Page	3 of 8
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Late Start	Late Finish	2019		2020		
A12810	Excavation (35.3 - 27.8mpd)	3	04-Feb-20	06-Feb-20	223	03-Nov-20	05-Nov-20	Dec	Jan Feb	Mar	Apr	May
A12820	Form temp working platform for soil nail	3	07-Feb-20	10-Feb-20	223	06-Nov-20	09-Nov-20	-				
			0710520	1010520		00110720	00110120		_		1	
A16060	ormation at SMP2 +23mpd Portal Area Excavation & Form temp working platform for soil nail at 21mpd	2	08-Jan-20	09-Jan-20	5	14-Jan-20	15-Jan-20				 	
A16070	GFRP Soil Nail at 21mpd -15nos (assume)	4	10-Jan-20	14-Jan-20	5	16-Jan-20	20-Jan-20					
A16090	GFRP Soil Nail at 19.5mpd -14nos (assume)	4	15-Jan-20	18-Jan-20	5	21-Jan-20	24-Jan-20	-			1 1 1 1	
A16100		2	21-Jan-20	22-Jan-20	4	01-Feb-20	03-Feb-20					
	Excavation & Form temp working platform for soil nail at 18mpd										; ;	
A16110	GFRP Soil Nail at 18mpd - 15nos (assume)	4	23-Jan-20	03-Feb-20	4	04-Feb-20	07-Feb-20					
A16130	GFRP Soil Nail at 16.5mpd -14nos (assume)	4	04-Feb-20	07-Feb-20	4	08-Feb-20	12-Feb-20		_		; ; ;	
A16140	Excavation & Form temp working platform for soil nail at 15mpd	2	10-Feb-20	11-Feb-20	3	13-Feb-20	14-Feb-20					
A16150	GFRP Soil Nail at 15mpd - 15nos (assume)	4	12-Feb-20	15-Feb-20	3	15-Feb-20	19-Feb-20		_		; ; ;	į
A16170	GFRP Soil Nail at 13.5mpd -14nos (assume)	4	17-Feb-20	20-Feb-20	3	20-Feb-20	24-Feb-20		_			
A16180	Excavation & Form temp working platform for soil nail at 11mpd	2	22-Feb-20	24-Feb-20	2	25-Feb-20	26-Feb-20		_		 	
A16190	GFRP Soil Nail at 11mpd -15nos (assume)	4	25-Feb-20	28-Feb-20	2	27-Feb-20	02-Mar-20		•	•	· · · · · · · · · · · · · · · · · · ·	
A16210	GFRP Soil Nail at 9.5mpd - 14nos (assume)	4	29-Feb-20	04-Mar-20	2	03-Mar-20	06-Mar-20				· i	
A16220	Excavation to 8mpd -SMP2 Portal Area	2	05-Mar-20	06-Mar-20	2	07-Mar-20	09-Mar-20			•		
A16230	Tunnel Workreadytostart SMP2 Portal Area	0		06-Mar-20	2		09-Mar-20	 	06-N		rtSMP2 Portal Area	
Retaining Wa	all for Main Portal										 	+
Retaining W											1 1 1	1
A13160	Temp access road formation	12	08-Jan-20	21-Jan-20	75	16-Apr-20	29-Apr-20					
A13170	Erect temp working platform for piling	24	22-Jan-20	25-Feb-20	75	02-May-20	29-May-20					
A13180	Pre-drilling work - RMP3	24	26-Feb-20	24-Mar-20	75	30-May-20	27-Jun-20		I		i	
A13190	Piling (Pre-bored H, 610mm, 33nos)-RMP3	102	25-Mar-20	30-Jul-20	388	22-Jul-21	20-Nov-21				1	
Retaining W	Vall RMP2										1	-
A13260	Temp access road formation	12	08-Jan-20	21-Jan-20	99	16-May-20	29-May-20				· j	
A13270	Erect temp working platform for pilling	24	22-Jan-20	25-Feb-20	99	30-May-20	27-Jun-20					
A13280	Pre-drilling work - RMP2	21	25-Mar-20	22-Apr-20	75	29-Jun-20	23-Jul-20				!	
Retaining W	/all RMP6 - CSD		1			1					1	+
A15320	CSD approval period (CSD)	195	01-Jun-19 A	12-Jan-20	777	23-Feb-22	27-Feb-22				· 	
A15350	Excavation & Form temp working platform for soil nail at 21mpd -CSD RMP6	2	08-Jan-20	09-Jan-20	1	09-Jan-20	10-Jan-20				· j	
A15360	GFRP Soil Nail at 20.5mpd - 8nos	2	10-Jan-20	11-Jan-20	1	11-Jan-20	13-Jan-20					
A15370	Welding soil nail head to H pile and testing	7	13-Jan-20	20-Jan-20	1	14-Jan-20	21-Jan-20				. <u> </u>	
A15380	Testing fortest nail at 20.5mpd	7	13-Jan-20	20-Jan-20	12	03-Feb-20	10-Feb-20	<u> </u>				
A15390	Excavation & Form temp working platform for soil nail at 17.5mpd - CSD RMP6	2	21-Jan-20	22-Jan-20	1	22-Jan-20	23-Jan-20		•		1	
A15400	GFRP Soil Nail at 17.5mpd -7nos	2	23-Jan-20	24-Jan-20	1	24-Jan-20	01-Feb-20					
A15410	Welding soil nail head to H pile and testing	7	01-Feb-20	08-Feb-20	1	03-Feb-20	10-Feb-20	 				
A15420	Testing for test nail at 17.5mpd	7	01-Feb-20	08-Feb-20	1	03-Feb-20	10-Feb-20	-				
A15430	Excavation & Form temp working platform for soil nail at 14.5mpd - CSD RMP6	2	10-Feb-20	11-Feb-20	1	11-Feb-20	12-Feb-20					
A15440	GFRP Soil Nail at 14.5mpd -8nos	2	12-Feb-20	13-Feb-20	1	13-Feb-20	14-Feb-20					
A15450	Welding soil nail head to H pile and testing	7	14-Feb-20	21-Feb-20	1	15-Feb-20	22-Feb-20	-				
A15450 ———————————————————————————————————		7			1							
	Testing for test nail at 14.5 mpd		14-Feb-20	21-Feb-20		15-Feb-20	22-Feb-20	<u> </u>				
A15462	Excavation & Form temp working platform for soil nail at 11.5mpd - CSD RMP6	2	22-Feb-20	24-Feb-20	1	24-Feb-20	25-Feb-20	_				
A15464	GFRP Soil Nail at 11.5mpd -6nos	2	25-Feb-20	26-Feb-20	1	26-Feb-20	27-Feb-20					

	in Sewage Treatment Works to Caverns (8-Jan-20)		Ot- d	l Fig. 1		onth Rolling Pi	<u> </u>						Page 4
y ID	Activity Name	Original Duration	Start	Finish	Total Floa	t Late Start	Late Finish	2019			2020 Mor		
A15466	Welding soil nail head to H pile and testing	7	27-Feb-20	05-Mar-20	1	28-Feb-20	06-Mar-20	Dec	Jan	Feb	Mar	Apr	
A15468	Testing for test nail at 11.5mpd	7	27-Feb-20	05-Mar-20	1	28-Feb-20	06-Mar-20						
A15490	Excavation from 11.5 to 8mpd - CSD RMP6	2	06-Mar-20	07-Mar-20	1	07-Mar-20	09-Mar-20						
A15495	Tunnel Workre ady to start - CSD RMP6	0		07-Mar-20	1		09-Mar-20				Mar-20 ♦ Tunnel Workre adyt		
A15510	Retaining Wall base (28m)-CSD RMP6	12	09-Mar-20	21-Mar-20	170	05-Oct-20	17-Oct-20				· · · · · · · · · · · · · · · · · · ·	!	
											·		
A15520	Retaining Wall wall structure to 7.5mpd - CSD RMP6	12	16-Mar-20	28-Mar-20	170	12-Oct-20	24-Oct-20					<u> </u>	
A15530	Retaining Wall wall structure to 16mpd -CSD RMP6	12	23-Mar-20	06-Apr-20	170	19-Oct-20	02-Nov-20						
A15550	Retaining Wall wall structure to 23mpd -CSD RMP6	12	30-Mar-20	16-Apr-20	170	27-Oct-20	09-Nov-20						
	III RMP5 - CSD (Tunnel Portal Area)									; ; 			
A15560	CSD approval period (CSD)	195	01-Jun-19 A	12-Jan-20	777	23-Feb-22	27-Feb-22					 	
A16240	Excavation & Form temp working platform for soil nail at 21mpd - CSD RMP5 (Tunnel Portal Area)	3	08-Jan-20	10-Jan-20	12	22-Jan-20	24-Jan-20						
A16250	GFRP Soil Nail at 21mpd -8nos	4	11-Jan-20	15-Jan-20	12	01-Feb-20	05-Feb-20						
A16260	Welding soil nail head to H pile and testing	8	16-Jan-20	24-Jan-20	12	06-Feb-20	14-Feb-20			· L			
A16270	Testing fortest nail at 21mpd	8	16-Jan-20	24-Jan-20	12	06-Feb-20	14-Feb-20						
A16280	Excavation & Form temp working platform for soil nail at 18mpd - CSD RMP5 (Tunnel	3	01-Feb-20	04-Feb-20	12	15-Feb-20	18-Feb-20						
A16290	Portal Area) GFRP Soil Nail at 18mpd - 2nos	1	05-Feb-20	05-Feb-20	12	19-Feb-20	19-Feb-20						
A16300	Welding soil nail head to H pile and testing	8	06-Feb-20	14-Feb-20	12	20-Feb-20	28-Feb-20						
A16310	Testing fortest nail at 18mpd	8	06-Feb-20	14-Feb-20	12	20-Feb-20	28-Feb-20						
A16360	Excavation from 18 to 14mpd - CSD RMP5 (Tunnel Portal Area)	3	15-Feb-20	18-Feb-20	12	29-Feb-20	03-Mar-20						
A16370	Excavation from 14 to 11.5mpd - CSD RMP5 (Tunnel Portal Area)	3	22-Feb-20	25-Feb-20	9	04-Mar-20	06-Mar-20						
											<u>.</u>		
A16375	Excavation from 11.5 to 8mpd - CSD RMP5 (Tunnel Portal Area)	2	06-Mar-20	07-Mar-20	1	07-Mar-20	09-Mar-20						
A16380	Tunnel Workreadyto start - CSD RMP5 (Tunnel Portal Area)	0		07-Mar-20	1		09-Mar-20			07-	Mar 20 ♦ Tunnel Workreadyt	ostapt-CSDRMP5 (Tunnel Po	
A16410	Retaining Wall base (18m) - CSD RMP5 (Tunnel Portal Area)	12	09-Mar-20	21-Mar-20	333	28-Apr-21	12-May-21						
A16420	Retaining Wall wall structure to 7.5mpd - CSD RMP5 (Tunnel Portal Area)	12	16-Mar-20	28-Mar-20	333	06-May-21	20-May-21						
A16430	Retaining Wall wall structure to 16mpd - CSD RMP5 (Tunnel Portal Area)	12	23-Mar-20	06-Apr-20	333	13-May-21	27-May-21						
A16450	Retaining Wall wall structure to 23mpd -CSD RMP5 (Tunnel Portal Area)	12	30-Mar-20	16-Apr-20	333	21-May-21	03-Jun-21			·			
Retaining Wa	IIIRMP5 - CSD									1		1	
A15800	CSD approval period (CSD)	206	01-Jun-19 A	23-Jan-20	766	12-Feb-22	27-Feb-22			·		-	
A16460	Excavation & Form temp working platform for soil nail at 21mpd - CSD RMP5 (Tunnel Portal Area)	1	08-Jan-20	08-Jan-20	349	20-Mar-21	20-Mar-21		·- I				
A16470	GFRP Soil Nail at 21mpd - 17nos	3	09-Jan-20	11-Jan-20	349	22-Mar-21	24-Mar-21		·-				
A16480	Welding soil nail head to H pile and testing	3	13-Jan-20	15-Jan-20	349	25-Mar-21	27-Mar-21						
A16490	Testing for test nail at 21mpd	3	13-Jan-20	15-Jan-20	356	06-Apr-21	08-Apr-21						
A16500	Excavation & Form temp working platform for soil nail at 18mpd - CSD RMP5 (Tunnel	1	16-Jan-20	16-Jan-20	349	29-Mar-21	29-Mar-21						
A16510	Portal Area) GFRP Soil Nail at 18mpd - 16nos	3	17-Jan-20	20-Jan-20	349	30-Mar-21	01-Apr-21		·-				
A16520	· · · · · · · · · · · · · · · · · · ·	3	21-Jan-20	23-Jan-20	349	06-Apr-21	08-Apr-21					!	
	Welding soil nail head to H pile and testing					·	·						
A16530	Testing for test nail at 18mpd	3	21-Jan-20	23-Jan-20	357	15-Apr-21	17-Apr-21			; 		; ; ;	
A16540	Excavation & Form temp working platform for soil nail at 16.5mpd - CSD RMP5 (Tunnel Portal Area)	1	24-Jan-20	24-Jan-20	349	09-Apr-21	09-Apr-21		0				
A16550	GFRP Soil Nail at 16.5mpd - 22nos	4	01-Feb-20	05-Feb-20	349	10-Apr-21	14-Apr-21						
A16560	Welding soil nail head to H pile and testing	3	06-Feb-20	08-Feb-20	349	15-Apr-21	17-Apr-21	T		_			
A16570	Testing for test nail at 16.5mpd	3	06-Feb-20	08-Feb-20	350	16-Apr-21	19-Apr-21						
A16580	Excavation from 16.5 to 14mpd - CSD RMP5 (Tunnel Portal Area)	1	10-Feb-20	10-Feb-20	349	19-Apr-21	19-Apr-21	<u> </u>		0			
	Excavation from 14 to 8mpd - CSD RMP5 (Tunnel Portal Area)	1	11-Feb-20	11-Feb-20	349	20-Apr-21	20-Apr-21						

Relocation of Sha Ti	n Sewage Treatment Works to Caverns (8-Jan-20)				3 Mc	onth Rolling Pr	ogramme					Pa	nge 5 of 8
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Late Start	Late Finish	2019			2020		
A16600	Retaining Wall base (42m)-CSD RMP5	12	12-Feb-20	25-Feb-20	349	21-Apr-21	05-May-21	Dec	Jan	Feb	Mar	Apr	May
A16610	Retaining Wall wall structure to 7.5mpd - CSD RMP5	18	17-Feb-20	07-Mar-20	349	26-Apr-21	17-May-21						
A16620	Retaining Wall wall structure to 16mpd -CSD RMP5	18	24-Feb-20	14-Mar-20	349	04-May-21	25-May-21						
A16640	Retaining Wall wall structure to 23mpd -CSD RMP5	18	04-Mar-20	24-Mar-20	349	13-May-21	03-Jun-21						
Tunnel													
Preliminary W	Vorks									1		1 1 1	
A11820	Update BAR (Blasting Assessment Report) - pre paration and submission	92	06-Sep-19A	24-Jan-20	189	01-Sep-20	17-Sep-20						
A11825	Blasting door design	32	20-Nov-19 A	01-Feb-20	188	31-Aug-20	17-Sep-20						
A11830	Blasting Permit/ License - Preparation and submission	50	03-Feb-20	31-Mar-20	188	18-Sep-20	18-Nov-20						
A11840	Method statement for tunnel works (Blasting)	50	02-Jan-20 A	03-Mar-20	212	28-Sep-20	18-Nov-20						
A11850	Blasting Permit License - review by Mines Department	30	01-Apr-20	12-May-20	188	19-Nov-20	23-Dec-20						
A12365	Application of CNP	52	04-Mar-20	09-May-20	233	14-Dec-20	22-Feb-21						
Soft Ground 4	10m, Tunnel Excavation by Drill and Break									1 1 1		1	
A11870	Long Canopy Tube (Ch143 - 163)	23	09-Mar-20	03-Apr-20	1	10-Mar-20	06-Apr-20						
A11880	Tunnel excavation (Ch143 - 163)	23	06-Apr-20	07-May-20	1	07-Apr-20	08-May-20						
Rigid Barriers										1			
Rigid Barrier I	BMP1												
A13425	Pending for Setting out information for BMP1 (RFI0025)	25	15-Nov-19 A	13-Jan-20	125	16-Jun-20	20-Jun-20					1	
A13430	Temp. Access Road Formation	38	14-Jan-20*	04-Mar-20	125	22-Jun-20	06-Aug-20						
A13440	Form temp working platform for soil nail	5	05-Mar-20	10-Mar-20	125	07-Aug-20	12-Aug-20						
A13450	Soil Nail at 33.6mpd (Rows D & TN2)-25nos	15	11-Mar-20	27-Mar-20	125	13-Aug-20	29-Aug-20						
A13460	Soil Nail at 32.1mpd (Rows C)-25nos	15	28-Mar-20	18-Apr-20	125	31-Aug-20	16-Sep-20						
Rigid Barrier I	BMP2											1	
A13565	Pending for Setting out information for BMP2 (RFI0024)	25	15-Nov-19 A	13-Jan-20	164	03-Aug-20	07-Aug-20					1	
A13570	Form temp working platform for soil nail -BMP2	5	14-Jan-20	18-Jan-20	164	08-Aug-20	13-Aug-20						
A13580	Soil Nail at 38mpd (Cd1-6 & TN2)-7nos-BMP2	6	20-Jan-20	01-Feb-20	164	14-Aug-20	20-Aug-20						
A13590	Soil Nail at 36mpd (Cc1-5)-5nos-BMP2	5	03-Feb-20	07-Feb-20	164	21-Aug-20	26-Aug-20						
A13600	Soil Nail at 34mpd (Cb1-5 & TN1)-6nos-BMP2	5	08-Feb-20	13-Feb-20	164	27-Aug-20	01-Sep-20						
A13610	Soil Nail at 32mpd (Ca1-4)-4nos-BMP2	5	14-Feb-20	19-Feb-20	164	02-Sep-20	07-Sep-20						
A13620	Form temp working platform for soil nail -BMP2	5	20-Feb-20	25-Feb-20	164	08-Sep-20	12-Sep-20					 	
A13630	Soil Nail at 32.1mpd (Rows H & TN4)-11nos-BMP2	8	26-Feb-20	05-Mar-20	164	14-Sep-20	22-Sep-20						
A13640	Soil Nail at 31.1mpd (Rows G)-12nos-BMP2	8	06-Mar-20	14-Mar-20	164	23-Sep-20	03-Oct-20						
A13650	Excavation (33.1-31mpd)-BMP2	5	16-Mar-20	20-Mar-20	164	05-Oct-20	09-Oct-20						
A13660	Form temp working platform for soil nail - BMP2	5	21-Mar-20	26-Mar-20	164	10-Oct-20	15-Oct-20						
A13670	Soil Nail at 30.1 mpd (Row F)-11nos-BMP2	8	27-Mar-20	06-Apr-20	164	16-Oct-20	24-Oct-20						
A13680	Soil Nail at 29.1mpd (Row E & TN3)-12nos -BMP2	8	07-Apr-20	18-Apr-20	164	27-Oct-20	04-Nov-20	 					
A13850	Soil Nail at 38mpd (Db1-9)-9nos	7	08-Jan-20	15-Jan-20	313	30-Jan-21	06-Feb-21	 					
A13860	Soil Nail at 36mpd (Da1-9 & TN4)-10nos	7	16-Jan-20	23-Jan-20	313	08-Feb-21	22-Feb-21						
Access Road	I to Portion 12 - Phase 1											1	
Bridge A										i 		1 1 1	
Piling												1	
A11210	Pile Test	26	23-Dec-19 A	24-Jan-20	2	10-Jan-20	03-Feb-20						
Abutment A1												 	
A11230	Excavation - Abutment A1	61	22-Oct-19A	06-Feb-20	24	12-Feb-20	05-Mar-20						

Relocation of Sha Ti	in Sewage Treatment Works to Caverns (8-Jan-20)				3 Mc	onth Rolling Pr	ogramme				Page 6 of 8
Activity ID	Activity Name	Original Duration	Start	Finish		Late Start	Late Finish	2019		2020	
A11240	Base slab - AbutmentA1	13	07-Feb-20	21-Feb-20	24	06-Mar-20	20-Mar-20	Dec	Jan Feb	Mar	Apr Ma
A11250	Abutment Wall - Abutment A1	31	22-Feb-20	28-Mar-20	24	21-Mar-20	02-May-20				<u> </u>
A11260	Backfill (~9m)-Abutment A1 (Coarse fill)	12	30-Mar-20	16-Apr-20	24	04-May-20	16-May-20				
Pier A2	In a read of					1					
A11340	ELS - Pier A2-1	12	01-Feb-20	14-Feb-20	8	11-Feb-20	24-Feb-20				
A11350	Excavation - PierA 2-1	12	15-Feb-20	28-Feb-20	8	25-Feb-20	09-Mar-20				
A11360	Pile cap - Pier A2-1	18	29-Feb-20	20-Mar-20	8	10-Mar-20	30-Mar-20				
A11370	ELS -Pier A2-2	13	15-Feb-20	29-Feb-20	13	02-Mar-20	16-Mar-20			=	
A11380	Excavation - PierA2-2	12	02-Mar-20	14-Mar-20	13	17-Mar-20	30-Mar-20				
A11390	Pile cap - Pier A2-2	18	21-Mar-20	15-Apr-20	8	31-Mar-20	24-Apr-20				
A11410	PierA 2-1	24	21-Mar-20	22-Apr-20	26	25-Apr-20	25-May-20				
Pier A3											
A11430	ELS -Pier A3-1	13	08-Jan-20	22-Jan-20	16	03-Feb-20	17-Feb-20				
A11440	Excavation - PierA3-1	12	23-Jan-20	12-Feb-20	16	18-Feb-20	02-Mar-20				
A11450	Pile cap - Pier A3-1	18	13-Feb-20	04-Mar-20	16	03-Mar-20	23-Mar-20				
A11460	ELS -Pier A3-2	13	01-Feb-20	15-Feb-20	25	02-Mar-20	16-Mar-20				
A11470	Excavation - PierA 3-2	12	17-Feb-20	29-Feb-20	25	17-Mar-20	30-Mar-20				
A11480	Pile cap - Pier A3-2	18	02-Mar-20	21-Mar-20	25	31-Mar-20	24-Apr-20				
A11500	PierA34	24	05-Mar-20	01-Apr-20	16	24-Mar-20	24-Apr-20				<u> </u>
A11510	PierA32	24	02-Apr-20	06-May-20	16	25-Apr-20	25-May-20				
Pier A4	ELS -PierA4-1	12	01 Feb 20	14 Feb 20	2	04 Fab 20	17-Feb-20				
A11520			01-Feb-20	14-Feb-20		04-Feb-20					
A11530	Excavation - PierA4-1	12	15-Feb-20	28-Feb-20	2	18-Feb-20	02-Mar-20			.	
A11540	Pile cap - Pier A4-1	18	29-Feb-20	20-Mar-20	2	03-Mar-20	23-Mar-20				
A11550	ELS - Pier A4-2	12	15-Feb-20	28-Feb-20	14	03-Mar-20	16-Mar-20				
A11560	Excavation - PierA4-2	12	29-Feb-20	13-Mar-20	14	17-Mar-20	30-Mar-20				
A11570	Pile cap - Pier A4-2	18	21-Mar-20	15-Apr-20	8	31-Mar-20	24-Apr-20				
A11590	PierA4-1	24	21-Mar-20	22-Apr-20	2	24-Mar-20	24-Apr-20				
Abutment A5											
A11310	Abutment Wall -Abutment A5	31	14-Dec-19 A	22-Jan-20	38	28-Feb-20	13-Mar-20				
A11320	Backfill (~7m)- Abu tment A5 (Coarse fill)	12	23-Jan-20	12-Feb-20	75	04-May-20	16-May-20		:		
A11330	Transition Slab -Abutment A5	7	13-Feb-20	20-Feb-20	75	18-May-20	25-May-20				
Parapet			<u> </u>			<u> </u>					
A11645	Steel Vehicle para pet ma nufa during	80	31-Mar-20	10-Jul-20	2	02-Apr-20	13-Jul-20				
Bridge B											
Abutment B1											
A11710	Abutment Wall -Abutment B1	24	14-Dec-19 A	14-Jan-20	45	07-Mar-20	13-Mar-20				
A11720	Backfill (~6m)-A butment B1 (Coalse Fill)	12	15-Jan-20	04-Feb-20	87	09-May-20	22-May-20				
A11730	Transition Slab -Abutment B1	6	05-Feb-20	11-Feb-20	87	23-May-20	29-May-20	<u> </u>			
Abutment B2											
A11760	Base slab - Abutment B2	12	15-Jan-20	04-Feb-20	51	21-Mar-20	03-Apr-20				
A11770	Abutment Wall -Abutment B2	24	05-Feb-20	03-Mar-20	51	06-Apr-20	08-May-20				
A11780	Backfill (~8m)-A butment B 2 (Coa se fill)	12	04-Mar-20	17-Mar-20	51	09-May-20	22-May-20	 			
	, , ,								į		

	in Sewage Treatment Works to Caverns (8-Jan-20)		+			onth Rolling Pr	<u> </u>						Page 7
/ ID	Activity Name	Original Duration	Start	Finish	Total Floa	t Late Start	Late Finish	2019			2020		
A11790	Transition Slab -Abutment B2	6	18-Mar-20	24-Mar-20	51	23-May-20	29-May-20	Dec	Jan	Feb	Mar	Apr	
						, , ,	, , ,			1			
Deck Structu A11800	Beam & Slab between Abutment B1 & B2	30	25-Mar-20	05-May-20	51	30-May-20	06-Jul-20						<u></u>
			20 11101 20	00 11.00		00 111.07 20	0000.20			1		1	
Parapet A16810	Steel Vehicle para pet ma nufa during	80	20-Jan-20	05-May-20	51	26-Mar-20	06-Jul-20						
	<u> </u>	80	20-Jan-20	034viay-20	31	20-Wai-20	00-501-20						
	for Access Road to Portion 12												
Retaining Wa	Piling (mini-pile, 30nos)-RMZ1 (bay 9-10)	23	02-Dec-19 A	13-Jan-20	11	21-Jan-20	01-Feb-20						
A13910	pile test - RMZ1 (bay 9-10)	26	14-Jan-20	19-Feb-20	11	03-Feb-20	03-Mar-20			1			
A13950	Footing & wall structure - RMZ1 (Bay 1-3, 0-22.5m)	50	14-Dec-19 A	20-Feb-20	0	08-Jan-20	20-Feb-20						
A13960	Backfill - RMZ1 (Bay 1-3, 0-22.5m)(~10m)	66	21-Feb-20	14-May-20	43	16-Apr-20	06-Jul-20					1	
A13962	Footing structure - RMZ1 (Bay 4-5, 22.5-37.5m)	10	21-Feb-20	03-Mar-20	0	21-Feb-20	03-Mar-20						
A13970	ELS -RMZ1 (Bay 6-10, 37.5-76.5m)	5	14-Jan-20	18-Jan-20	27	21-Feb-20	26-Feb-20						
A13980	Excavation - RMZ1 (Bay 6-10, 37.5-76.5m)	5	20-Jan-20	24-Jan-20	27	27-Feb-20	03-Mar-20	 					
A13990	Footing & wall structure - RMZ1 (Bay 6-10, 37.5-76.5m)	73	04-Mar-20	03-Jun-20	0	04-Mar-20	03-Jun-20	-					
			OT IVIGI 20	00 0011 20		OT Mai 20	00 0011 20			1 1 1		1	
Retaining Wa	Piling (mini-pile, 48nos)-RMZ2 (bay 2-8)	48	13-Mar-20	14 May 20	50	49 May 20	14-Jul-20				· · · · · · · · · · · · · · · · · · ·		
				14-May-20		18-May-20							
A14080	Piling (mini-pile, 100nos)-RMZ2 (bay 10-18)	50	08-Jan-20	12-Mar-20	8	17-Jan-20	21-Mar-20						
A14090	pile test - RMZ2 (bay 10-18)	26	13-Mar-20	16-Apr-20	8	23-Mar-20	25-Apr-20						
Cut Slope SM	IZ1												
A14360	Excavation - Cut Slope SMZ1	12	21-Feb-20	05-Mar-20	69	19-May-20	01-Jun-20						
A14370	Slope formation - Cut Slope SMZ1	21	06-Mar-20	30-Mar-20	69	02-Jun-20	26-Jun-20					=	
Cut Slope SM	IZ5									1		1	
A14440	Excavation - Cut Slope SMZ5	19	23-Jan-20	20-Feb-20	96	28-May-20	18-Jun-20						
A14450	Slope formation - Cut Slope SMZ5	31	21-Feb-20	27-Mar-20	96	19-Jun-20	27-Jul-20						
Cut Slope SM	176		<u> </u>										
A14460	Excavation (162 -156 mpd)-SMZ6	11	23-Jan-20	11-Feb-20	38	14-Mar-20	26-Mar-20						
A14470	Form temp working platform for soil nail - SMZ6	4	12-Feb-20	15-Feb-20	38	27-Mar-20	31-Mar-20	-					
A14480	Soil Nail at 154mpd (D1-9 & TN4)-10nos-SMZ6	6	17-Feb-20	22-Feb-20	38	01-Apr-20	08-Apr-20	-					
						·					<u></u>		
A14490	Soil Nail at 152mpd (C1-9 & TN3)-10nos-SMZ6	6	24-Feb-20	29-Feb-20	38	09-Apr-20	18-Apr-20						
A14500	Slope & berm formation - SMZ6	31	02-Mar-20	07-Apr-20	38	20-Apr-20	27-May-20						
Cut Slope SM										; ;			
A14600	Excavation - Cut Slope SMZ8	19	08-Jan-20	05-Feb-20	65	31-Mar-20	25-Apr-20			1			
A14610	Slope formation - Cut Slope SMZ8	31	06-Feb-20	12-Mar-20	182	15-Sep-20	22-Oct-20						
A14810	Maintenance staircase & stepped channel - SMZ8	25	13-Mar-20	15-Apr-20	287	06-Mar-21	07-Apr-21						
Road Works													
	om A Kung Kok Shan Road to Bridge A									1 1 1		1 1 1	
A14860	400 dia contrete pipe around the road besides SMZ2	19	21-Feb-20	13-Mar-20	90	12-Jun-20	06-Jul-20						
Access Road	d to Portion 12 - Phase 2												
Road Works													
	A Kung Kok Shan Road Roundabout											<u> </u>	
A15230	Demolish existing footpath at A Kung Kok Shan Road Roundabout	6	08-Jan-20	14-Jan-20	366	13-Apr-21	19-Apr-21					·	
A15240	Demolish existing planter at Cul-De-Sac	6	15-Jan-20	21-Jan-20	366	20-Apr-21	26-Apr-21						
	Ţ.		1			'						1	;

Relocation of Sha Tin Sewage Treatment Works to Caverns (8-Jan-20)					3 Mo	nth Rolling Pro	ogramme					P	Page 8	
y ID	Activity Name	Original Duration	Start	Finish	Total Float	Late Start	Late Finish	2019		2020				
		Buildion	'					Dec	Jan	Feb	Mar	Apr		
Tree Treatm	ent									1				
Tree Treatr	ment													
A11052	Tree transplant (Portion 8)	91	08-Jan-20	06-May-20	213	29-Sep-20	19-Jan-21							
A11060	Tree felling & protection (Portion 10)	61	08-Jan-20	25-Mar-20	152	20-Jul-20	28-Sep-20							
A12400	Tree transplant (Portion 10)	91	26-Mar-20	18-Jul-20	152	29-Sep-20	19-Jan-21	-		i 		<u> </u>		
Community I	Liaison Centre													
Design Design	LIABOTT OCTIVE													
A16720	Community Liaison Centre Design approval (Architectual)	111	27-Aug-19A	15-Jan-20	63	11-Mar-20	18-Mar-20			: 				
	<u> </u>									! !				
A16740	Community Liaison Centre Design approval (Drainage & E&M)	68	09-Oct-19A	15-Jan-20	77	25-Mar-20	01-Apr-20							
A16750	Community Liaison Centre Design Preparation (Landscape)	59	09-Oct-19 A	15-Jan-20	36	26-Feb-20	04-Mar-20			1				
A16760	Community Liaison Centre Design approval (Landscape)	21	16-Jan-20	05-Feb-20	49	05-Mar-20	25-Mar-20							
Community	y Liaison Centre	'	-							1				
A10150	G/F slab	12	12-Dec-19 A	21-Jan-20	55	19-Mar-20	01-Apr-20							
A10154	Shop Drawing approval	21	06-Jan-20 A	14-Jan-20	0	08-Jan-20	14-Jan-20			; 				
A10160	Off-site factory fabrication	49	15-Jan-20	18-Mar-20	0	15-Jan-20	18-Mar-20			1				
A10170	Material dilivery on site	6	19-Mar-20	25-Mar-20	0	19-Mar-20	25-Mar-20					- 		
A10180	On stie installation (MIC)	20	26-Mar-20	22-Apr-20	6	02-Apr-20	29-Apr-20							
A10210	Feature Fence	21	26-Mar-20	23-Apr-20	0	26-Mar-20	23-Apr-20			L			 I	
A10220	Portable Planter	21	26-Mar-20	23-Apr-20	0	26-Mar-20	23-Apr-20						 1	
Portion 10 - 0	Coreboxes Containers Area													
	- Coreboxes Containers Area									1				
A10530	Demolished existing structure	32	26-Mar-20	08-May-20	211	10-Dec-20	19-Jan-21			1				
