



Environmental Permit (No. EP-537/2017)

19 February 2018

The EIA Ordinance Register Office,
Environmental Protection Department,
27th floor, Southorn Centre,
130 Hennessy Road,
Wanchai, Hong Kong

By Hand & Fax
(fax no. 2591 0558)

Attn: Director of Environmental Protection

Dear Sir/ Madam,

**Expansion of Research and Residential Facilities for
The Swire Institute of Marine Science, Faculty of Science,
The University of Hong Kong at Cape d' Aguilar, Shek O, Hong Kong
Submission of Monthly Environmental Monitoring and Audit Report No.4**

Refer to the Environmental Permit No. EP-537/2017 under Environmental Impact Assessment Ordinance (Chapter 499) Section 10.

We are pleased to submit three hard copies and three electronic copies of the monthly environmental monitoring report certified by the IEC in responded to the Specific Conditions 2.3 of the Environmental Permit (No. EP-537/2017).

Should you have any queries, please feel free to contact our Mr Cliff Ip at 2957 9611.

Thank you for your attention.

Yours faithfully
For and on behalf of
Percy Thomas Partnership (HK) Ltd.

Vetus T C Lau
Authorized Person

VL/CI/31122(1)31.3/ Z000547

P:\31122 Swire Institute of Marine Science\Correspondence\Letter\EPD\2018-2-19 IEC report.docx

Encl.

CC

The University of Hong Kong

- Mr John Sung w/o (Fax: 2517 0456)

- Mr K B Wong

Wong & Cheng Consulting Engineers Ltd

- Mr Sammy Cheng w/o (Fax: 2865 6610)

- Mr Simon Yu

Arcadis

- Mr Kong Li w/o (Fax: 2805 5028)

Acuity Sustainability Consulting Limited

- Mr Jacky Leung w/o (Fax: 2333 1316)

- Mr Kevin Li



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
Temporary Office: Lot 12, Tam Kon Shan Road, Tsing Yi, N.T.
Tel.: (852) 2333 6823 Fax.: (852) 2333 1316

MONTHLY ENVIRONMENTAL MONITORING AND AUDIT (EM&A) REPORT (NO. 4)

FOR

**Expansion of Research and Residential Facilities for the Swire Institute of
Marine Science, The University of Hong Kong at Cape D'Aguiar, Shek O**

(Rev. 0)

**MONTHLY ENVIRONMENTAL
MONITORING AND AUDIT
(EM&A) REPORT (NO.4) -**

FOR

**EXPANSION OF RESEARCH AND RESIDENTIAL
FACILITIES FOR THE SWIRE INSTITUTE OF
MARINE SCIENCE**




| | Name | Signature |
|--------------------------|---|---|
| Prepared by | Ms. Cheung, Karen, K.Y. |  |
| Checked & Reviewed by | Mr. Tsui, Nelson, T. H. |  |
| Approved by | Mr. Li, Kevin, W. M. Independent Environmental Checker (IEC) |  |

TABLE OF CONTENTS

EXECUTIVE SUMMARY

1. INTRODUCTION

- 1.1 PROJECT BACKGROUND**
- 1.2 ORGANIZATION STRUCTURE**
- 1.3 SCOPE OF REPORT**
- 1.4 SUMMARY OF CONSTRUCTION WORKS**

2. EM&A RESULTS

- 2.1 EM&A BACKGROUND**
- 2.2 ENVIRONMENTAL LICENSES AND PERMITS**
- 2.3 IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES**
- 2.4 EM&A SITE INSPECTIONS**
- 2.5 SUMMARY IF EXCEEDANCES OF ENVIRONMENTAL QUALITY PERFORMANCE LIMIT**

3. FUTURE KEY ISSUES

- 3.1 CONSTRUCTION PROGRAMME FOR COMING MONTHS**
- 3.2 KEY ISSUES FOR THE COMING MONTH**

4. CONCLUSIONS AND RECOMMENDATIONS

- 4.1 SUMMARY**

LIST OF APPENDICES

| | |
|------------|--|
| Appendix A | Location of Construction Activities |
| Appendix B | Project Organization |
| Appendix C | Cumulative Statistics on, Complaints, Notifications of Summons and Successful Prosecutions |
| Appendix D | Environmental Monitoring Checklist |

EXECUTIVE SUMMARY

- A.1 Pursuant to the Environmental Impact Assessment (EIA) Ordinance, the Director of Environmental Protection (“DEP”) granted the Environmental Permit (No. EP- 537/2017) to The University of Hong Kong (“HKU”) to construct and operate the designated project for “Extension of Academic Block, The Swire Institute of Marine Science, Faculty of Science, The University of Hong Kong, Cape D’Aguilar Road, Shek O” (“The Project”).
- A.2 Seemly Building Construction Company Limited (“SBC”) is commissioned by HKU to undertake the construction of the extension works while Percy Thomas Partnership (HK) Limited (“PTP”) was appointed by HKU as the Architect. For implementation of the environmental monitoring and audit (EM&A) requirement under the Project Profile, Acuity Sustainability Consulting Limited (“ASC”) was appointed by PTP as the Independent Environmental Checker (IEC).
- A.3 The construction phase of the Contract commenced on 6 October 2017 for completion by end of 2018. The environmental site inspections of the EM&A programme commenced on October 2017.
- A.4 This is the 4th monthly Environmental Monitoring and Audit Report for this Contract covering the period from 6 January 2018 to 5 February 2018 (the Reporting Period). As informed by the Contractor, major activities in the reporting period included:
- Demolition Works
 - Spalling Concrete Repair
 - A&A Works
 - Fitting Out Works
 - BS First Fixing
 - Waterproofing works at Roof
- A.5 IEC Monthly Environmental Site Audit under the EM&A requirement in this reporting period was conducted on 18 January 2018.
- A.6 No environmental complaint was received via EPD in this reporting period.
- A.7 No notification of any summons and successful prosecutions was received in this reporting period.
- A.8 No reporting change was made in this reporting period.
- A.9 As informed by the Contractor, the major works for this Project in February 2018 will be:
- Waterproofing works at Roof
 - Block Wall erection
 - A&A Works
 - Fitting Out Works
 - BS Fixing
 - Painting
 - Window replacement
- A.10 EM&A monitoring for the 4th reporting period has been completed. The 5th monthly EM&A report will cover the period from 6 February 2018 to 5 March 2018.

1. INTRODUCTION

1.1. PROJECT BACKGROUND

- 1.1.1. Pursuant to the Environmental Impact Assessment (EIA) Ordinance, the Director of Environmental Protection (“DEP”) granted the Environmental Permit (No. EP- 537/2017) to The University of Hong Kong (“HKU”) to construct and operate the designated project for “Extension of Academic Block, The Swire Institute of Marine Science, Faculty of Science, The University of Hong Kong, Cape D’Aguilar Road, Shek O” (“The Project”).
- 1.1.2. Seemly Building Construction Company Limited (“SBC”) is commissioned by HKU to undertake the construction of the extension works while Percy Thomas Partnership (HK) Limited (“PTP”) was appointed by HKU as the Architect. For implementation of the environmental monitoring and audit (EM&A) requirement under the Project Profile, Acuity Sustainability Consulting Limited was appointed by PTP as the Independent Environmental Checker (IEC).
- 1.1.3. The construction phase of the Contract commenced on 6 October 2017 for completion by end of 2018. The general layout plan of the Contract components is presented in Appendix A.

1.2. ORGANIZATION STRUCTURE

1.2.1. The organization structure of the Contract is shown in Appendix B. Contact details of key personnel are summarized in below table:

Table 1-1: Key Personnel Contact for Environmental Works

| Party | Position | Name | Telephone |
|--|---|------------------|------------------|
| The University of Hong Kong | Assistant Director | John Sung | 2816 8208 |
| Seemly Building Construction Co., Ltd. | Project Manager | Mr. S.K. Fan | 6532 3490 |
| Percy Thomas Partnership (HK) Ltd | Senior Architect | Cliff Ip | 2957 9611 |
| | Architectural Assistant | Bertinla Lai. | 2957 9605 |
| Acuity Sustainability Consulting Limited | Independent Environmental Checker (IEC) | Li, Kevin, W. M. | 2333 6823 |

1.3. SCOPE OF REPORT

1.3.1. This is the 4th monthly IEC Report for “Extension of Academic Block, The Swire Institute of Marine Science, Faculty of Science, The University of Hong Kong, Cape D’Aguilar Road, Shek O” covering the period from 6 January 2018 to 5 February 2018 (the reporting period).

1.3.2. The EM&A requirements for impact monitoring are set out in the approved Project Profile (Register No. PP-548/2017). All mitigation measures recommended in the Project Profile such as the construction air quality, noise, water quality, waste management, landscape and visual, cultural heritage and ecology were identified as the key issues during the construction phase of the Project.

1.4. SUMMARY OF CONSTRUCTION WORKS

1.4.1. The construction phase of the Contract commenced on 6 October 2017.

1.4.2. As informed by the Contractor, details of the major works carried out in this reporting month are listed below:

- Waterproofing works at Roof
- Block Wall erection
- A&A Works
- Fitting Out Works
- BS Fixing
- Painting
- Window replacement

1.4.3. The locations of the construction activities are shown in Appendix A.

2. EM&A RESULTS

2.1. EM&A BACKGROUND

2.1.1. The Environmental Permit (No. EP-537/2017) required Independent Environmental Checker (IEC) to certify the implementation status of mitigation measures in a monthly audit report during the construction of the Project. Environmental site inspection for air quality, noise, water quality, waste management and ecology mitigation measures was conducted on 18 January 2018. A summary of mitigation measure is presented in Table 2-2.

2.1.2. The monitoring checklist is shown in Appendix D.

2.2. ENVIRONMENTAL LICENSES AND PERMITS

2.2.1. The status of environmental license and permit is summarized in Table 2-2 below:

Table 2-1: Summary of Environmental License and Permit

| License / Permit | License / Permit No. | Date of Issue | Date of Expiry | License / Permit Holder | Remark |
|---------------------------------|----------------------|---------------|----------------|-------------------------|--------|
| Environmental Permit | EP-537/2017 | 18/05/2017 | N/A | HKU | |
| Billing Account | Account No. 7027765 | 10/05/2017 | - | SBC | |
| Waste Water Discharge License | - | - | - | - | N/A |
| Chemical Waste Producer | 5292-197-S3753-02 | 01/12/2017 | - | SBC | - |
| Air Pollution Control Ordinance | Ref. No. 422086 | 12/10/2017 | - | SBC | - |
| Construction Noise Permit | - | - | - | - | N/A |

2.3. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

2.3.1. In response to the Project Profile (Registar No. PP-548/2017). The status of the environmental mitigation measures implemented by the Contractor in this Reporting Period was audit on 18 January 2018 and the checklist is showed in Appendix D.

2.3.2. The environmental mitigation measures that recommended in the project profile and environmental permit covered the issues of dust, noise, air quality, water, ecology, landscape and visual, cultural heritage and waste management and they are showed Table 2-2.

Table 2-2: Environmental Mitigation Measures

| Issues | Environmental Mitigation Measures |
|-------------|--|
| Air Quality | <ul style="list-style-type: none"> - Erection of hoarding of not less than 2.4m high from ground level along the works area that adjoins a road or other area accessible to the public, where appropriate; - The works area of any excavation or earth moving operation shall be sprayed with water to maintain the entire surface wet; - All dusty materials shall be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet; - Cover stockpile of dusty materials by impervious sheeting or sprayed with water so as to maintain the entire surface wet or removed or backfilled within 24 hours of the excavation or unloading; - Any debris shall be covered entirely by impervious sheeting or stored in a debris collection area sheltered on the top and the 3 sides; - Ultra Low Sulphur Diesel (ULSD i.e. Sulphur content not more than 0.005%) should be used for all the onsite PME; - Every vehicle shall be washed to remove any dusty materials from its body and wheels; - Where a vehicle leaving the construction works area is carrying a load of dusty materials, the load shall be covered by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle; - Unpaved road shall be regularly compacted and the road surface shall be kept clear of loose materials; - The speed of all vehicles moving within the Site shall be restricted to minimize fugitive dust emission; - All on-site PME shall be well-maintained and operated in a good manner that no black smoke will be emitted; and - No PME in operation that any black smoke is emitted for more than 6 minutes in any period of 4 hours or for more than 3 minutes continuously at any one time. |
| Noise | <ul style="list-style-type: none"> - Care in the placement and orientation of noisy plants away from the NSRs and effective utilization of material stockpiles and other structures in screening noise from the on-site construction activities; - Careful planning of construction sequence; - The operation time of noisy PME should be kept at minimum; - Hoarding will be erected along the site boundary for noise screening purpose; - Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program; - All hoods, cover panels and inspection hatches of power mechanical plant such as generator, air compressor etc. should be closed during operation; - Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; - Utilization of silencers or mufflers on the construction equipment to reduce noise without impairing machine efficiency, |
| Water | <ul style="list-style-type: none"> - Contractor shall obtain construction site discharge license from the EPD under WPCO; - To prevent sewage from entering the inland water and inshore water, hoardings will be erected along the site boundary. Surface run-off from construction site shall be treated via adequately designed sand/silt |

| | |
|---|--|
| | <p>removal facilities such as sand traps, silt traps and sedimentation tank or STP first to prevent sewage from entering the inland water and inshore water, and then collected by licensed collector and discharged off site;</p> <ul style="list-style-type: none"> - The vehicle washing bay shall be located on paved area and away from the sensitive receivers and provided with a suitable backfill to prevent the site run-off from entering the public roads; - All water used on site shall be re-circulated and re-used for beneficial uses as dust suppression, wheel washing and general cleaning; - Online standby water sump pumps of sufficient capacity and with automatic devices shall be provided to prevent overflow of sewage from any water recycling system; - Open stockpiles of construction materials on site or exposed earth surface shall be avoided as far as practicable or, where unavoidable, should be covered with impervious sheet such as tarpaulin sheet or similar fabric during rainstorms; - Stagnant water shall be removed every day. Extra pumps shall be used to pump the water into sedimentation tank during rainy days when necessary; - Earth bund or sand bag barriers shall be provided onsite to properly direct storm water to the silt removal facilities such as sedimentation tank provided; - Good site practices shall be adopted to remove rubbish and litter from construction site to prevent the rubbish and litter from spreading from the site area. It is recommended to clean the construction sites on a regular basis; - Sufficient chemical toilets shall be provided in the works area and a licensed waste collector should be deployed to clean the chemical toilets on a regular basis; - Notices shall be posted at conspicuous locations to remind the workers not to discharge any sewage or sewage into the nearby environment; and - It is recommend that the Contractor include the sewage control measures during their onsite toolbox talk to increase the awareness of all workers. |
| <p style="text-align: center;">Waste Management</p> | <ul style="list-style-type: none"> - Construction works shall be carefully planned to minimize the amount of wastes generated and avoid unnecessary generation of wastes; - Sufficient waste disposal points and regular collection of wastes shall be provided; - Different types of wastes shall be segregated and stored properly to promote reuse or recycling; - Dump truck leaving the Site shall be covered properly with impervious sheeting; - Contractor shall register as a Chemical Waste Producer if chemical wastes such as spent lubricants are generated onsite. All chemical waste shall be properly handled, stored, labeled, packaged and collected in accordance with the requirements of the Waste Disposal (Chemical Waste) (General) Regulation; - Surplus C&D materials (inert and non-inert) generated from the proposed works requiring disposal shall be properly transported to the designated disposal facilities managed by CEDD and EPD. A trip-ticket system shall be implemented by the Contractor and monitored as a standard item in the relevant technical audit, in accordance with the requirements specified in DEVB TC(W) No. 6/2010 Trip Ticket System |

| | |
|----------------------|---|
| | <ul style="list-style-type: none"> - for Disposal of Construction & Demolition Materials; - Waste Management Plan shall be prepared in accordance with the requirement specified in Building Departments Practice Note for Authorized Persons and Registered Structural Engineers – Construction and Demolition Waste (ADV-19); - Toolbox talks shall be arranged to workers on relevant topics including site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling. |
| Ecology | <ul style="list-style-type: none"> - Access route and placement of equipment and stockpile in works area shall be selected at existing developed area and disturbed land to minimize disturbance on vegetation. The chosen temporary storage or stockpiling area and access routes shall be far away from any identified plant species of conservation importance; - Construction activities will be restricted to the clearly defined works area; - Temporary works area will be reinstated immediately after completion of the construction works; - Disposal and treatment of waste shall be carried out in a timely and proper manner - Open fires will be strictly prohibited to prevent any risk of wildfire; - Fire-fighting equipment should be provided in the works area before the commencement of works and - Resident site personnel shall ensure the Implementation of the mitigation measures |
| Landscape and Visual | <ul style="list-style-type: none"> - Design with minimum vegetation clearance - Compensatory planting of native trees and shrubs - Retain and preserve all plant species of conservation importance on site - Amenity value improved by compensatory planting and natural regeneration of plants - Erection of hoarding with colour compatible to the surrounding around works areas |
| Cultural Heritage | <ul style="list-style-type: none"> - No-entry zone will be fenced off by eye-catching net at the Cape D' Aguilar Lighthouse - Placement of equipment and stockpile at the road section close to the Lighthouse are prohibited - Using manual gear for trenching work near the Lighthouse - Monitor the vibration near the Lighthouse |


2.3.3. The necessary mitigation measures were implemented properly for this Contract in the reporting period.





2.4. EM&A SITE INSPECTION

2.4.1. Site inspection was carried out on a monthly basis to monitor the implementation of mitigation measures under the Contract. In the reporting period, site inspections were carried out on 18 January 2018.

2.4.2. Minor deficiencies were observed during site inspection. Key observations during the site inspections are summarized in Table 2-3.

Table 2-3: Site Observations

| Date | Environmental Observations | Follow-up Status |
|-------------|---|---|
| 18-Jan-2018 | Broken Concretes was found at the facade of Academic Block | Rectified by contractor on 19-Jan-2018 Broken Concretes was removed |
| |  |  |
| 18-Jan-2018 | Gap between noise curtain was spotted, which it might affect the noise reduction | Rectified by contractor on 20-Jan-2018 Ties were installed between the noise curtains to link up the curtains. |
| |  |  |

| Date | Environmental Observations | Follow-up Status |
|-------------|---|---|
| 18-Jan-2018 | Waste was found inside the orange net in Site C | Rectified by contractor on 20-Jan-2018 Waste was removed. |
| |  |  |
| 18-Jan-2018 | Dried <i>Vitis bryoniifolia</i> was found | Rectified by Contractor on 22 January 2018 Inspection was carried out with Qualified Ecologist on 22-Jan-2018. Dried leaf of <i>Vitis bryoniifolia</i> was found and no green leaf was observed. |
| |  |  |

2.4.3. The Contractor has rectified all observations identified during environmental site inspection in the reporting period.

2.5. SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS

2.5.1. The Environmental Complaint Handling Procedure is shown in below table:

Table 2-4: Environmental Complaint Handling Procedure

| | |
|--|---|
| Complaint Received via Liaison Officer | Complaint Received via 1823 or from other government departments |
| SBC notify PTP, HKU and IEC | SBC notify PTP ,HKU, and IEC |
| Register of the complaint. SBC to conduct investigation of complaint and report to HKU,PTP and IEC the investigation results | |
| If complaint is considered not valid | If complaint is found valid |
| HKU or SBC to reply the complainant if necessary | SBC to implement necessary improvement measures in consultation with the IEC, HKU and PTP. HKU to check and inspect if the situation is improved. IEC to conduct further inspection as necessary. |
| | HKU to report the follow up actions done by SBC and reply to complainant is necessary. If the complaint is referred by the EPD, SBC to prepare interim report on the status of the complaint investigation and follow-up action |
| SBC prepare complaint report for submission to EPD and to record the complaint case in monthly EM&A report | |

2.5.2. No environmental complaint was received in the reporting period.

2.5.3. No notification of summons and prosecution was received in the reporting period.

3. FUTURE KEY ISSUES

3.1. CONSTRUCTION PROGRAMME FOR THE COMING MONTHS

3.1.1. As informed by the Contractor, the major works for this Project in February 2018 will be:

- Waterproofing works at Roof
- Block Wall erection
- A&A Works
- Fitting Out Works
- BS Fixing
- Painting
- Window replacement

3.2. KEY ISSUES FOR COMING MONTH

3.2.1. Potential environmental impacts arising from the above upcoming construction activities in February 2018 are mainly associated with air quality, noise, water quality, waste management and ecology issues.

3.2.2. Particular issues to be considered in the coming month include:


- Implementation of construction noise preventative control measures.
- Implementation of construction dust prevention control measure

4. CONCLUSIONS AND RECOMMENDATIONS


4.1. SUMMARY

- 4.1.1. Inspection was carried out on 18 January 2018. Minor deficiencies were observed during site inspection and were rectified within the reporting period. Some mitigation measures were not applicable for the current construction stage, the mitigation measures were implemented properly in general. The environmental performance of the Project was therefore considered satisfactory.
- 4.1.2. To control the site performance of noise level, the contractor shall ensure that the noise barrier should be adopted during works. Contractor is also reminded to implement the recommended environmental mitigation measures according to the Project profile and Environmental Permit.
- 4.1.3. During the joint site inspection, *Vitis bryoniifolia* was found dried. The condition of *Vitis bryoniifolia* is being concerned and contractor is reminded to inspect the condition more frequent.
- 4.1.4. No environmental complaint was received in the reporting period.
- 4.1.5. No notification of summons or prosecution was received since commencement of the Contract.
- 4.1.6. SBC will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Appendix A : Location of Construction

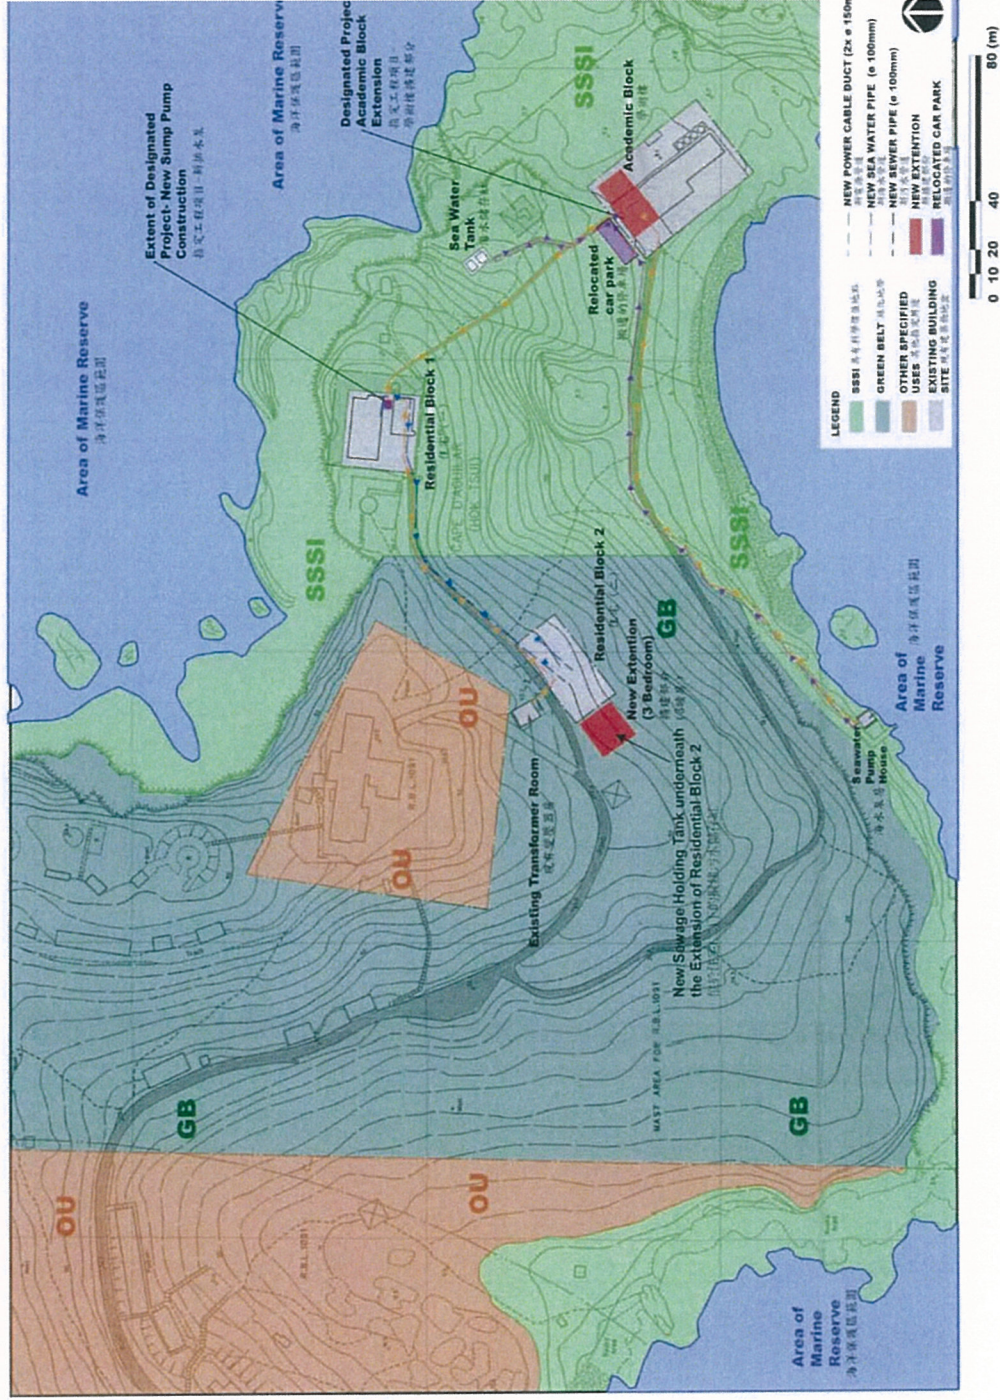

Appendix B: Project Organization

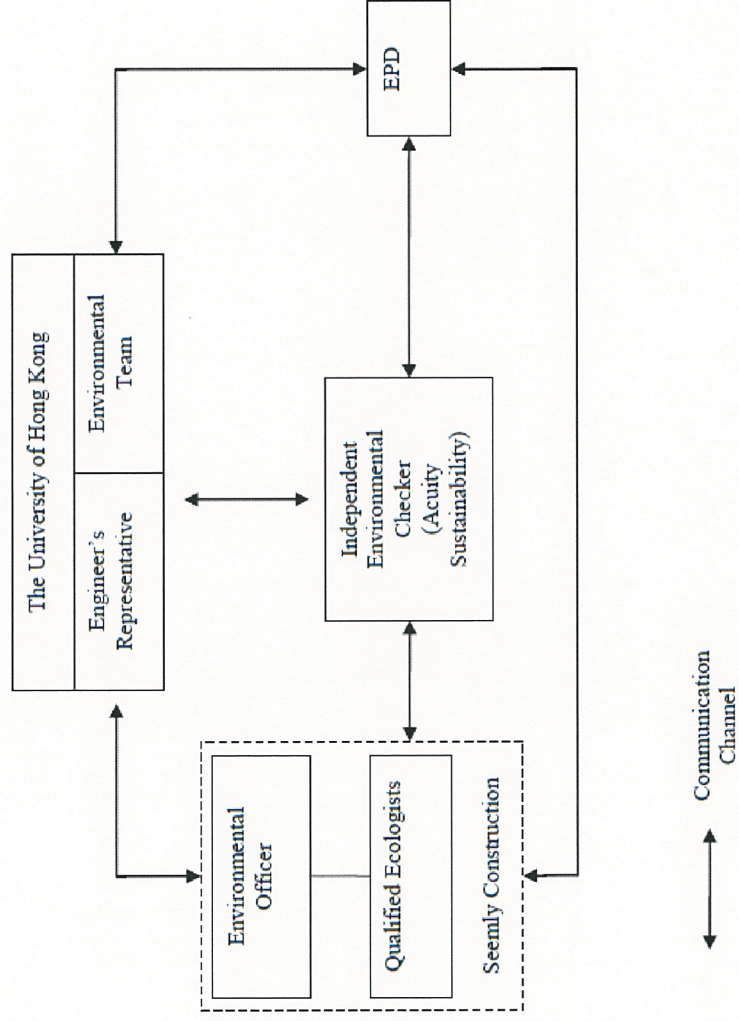

Appendix C: Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Statistical Summary of Environmental Complaints

| Reporting Period | Environmental Complaint Statistics | | |
|---------------------------|------------------------------------|------------|------------------|
| | Frequency | Cumulative | Complaint Nature |
| 6 Jan 2018- 5 Feb 2018 | 0 | 0 | N/A |

Statistical Summary of Environmental Summons

| Reporting Period | Environmental Summons Statistics | | |
|---------------------------|----------------------------------|------------|---------|
| | Frequency | Cumulative | Details |
| 6 Jan 2018- 5 Feb 2018 | 0 | 0 | N/A |

Statistical Summary of Environmental Prosecution

| Reporting Period | Environmental Prosecution Statistics | | |
|---------------------------|--------------------------------------|------------|---------|
| | Frequency | Cumulative | Details |
| 6 Jan 2018- 5 Feb 2018 | 0 | 0 | N/A |

Appendix D: Environmental Monitoring Checklist



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

In-situ Provisioning of Proposed Extension of Academic Block, The Swire Institute of Marine Science, Faculty of Science, The University of Hong Kong, Cape D'Aguiar Road, Shek O

| | |
|--------------------|--|
| Inspection Date: | 18 Jan, 2018 |
| Inspected by: | IEC: Nelson Tsui, Karen Cheung PTP: Cliff Ip. SM SBC: Ken Wong, |
| Inspection Time: | 2:00 p.m. |
| Weather Condition: | Sunny |
| Temperature: | 19.4 |
| Wind: | 22 km/hr |

| | | N/A | Yes | No | Remarks |
|-----------------------|--|-----|-----|----|------------------|
| 1. Noise | | | | | |
| 1.1 | Is the placement and orientation of noisy plants away from the NSRs in screening noise from the on-site construction activities? | ✓ | | | |
| 1.2 | Is the construction sequence carefully planned? | | ✓ | | |
| 1.3 | Is the operation time of noisy PME keep at minimum? | ✓ | | | |
| 1.4 | Are the hoarding erected along the site boundary for noise screening purpose? | ✓ | | | observation ② |
| 1.5 | Do all plants operate on-site are well-maintained? | ✓ | | | |
| 1.6 | Do all plants service regularly during the construction program? | ✓ | | | |
| 1.7 | Do all hoods, cover panels and inspection hatches of power mechanical plant close during operation? | ✓ | | | |
| 1.8 | Are the machines and plant shut down between work periods or throttled down to a minimum? | ✓ | | | |
| 2. Air Quality | | | | | |
| 2.1 | Is the erection of hoarding not less than 2.4m high from ground level along the works area? | ✓ | | | |
| 2.2 | Is the hoarding not adjoined a road or other area accessible to the public? | ✓ | | | |

**In-situ Provisioning of Proposed Extension of Academic Block,
The Swire Institute of Marine Science,
Faculty of Science, The University of Hong Kong,
Cape D'Aguilar Road, Shek O**

| | | N/A | Yes | No | Remarks |
|------|---|-----|-----|----|---------|
| 2.3 | Is the excavation or earth moving operation in the site sprayed with water to maintain the entire surface wet? | ✓ | | | |
| 2.4 | Are all dusty materials sprayed with water prior to any loading, unloading or transfer operation to maintain the dusty materials wet? | ✓ | | | |
| 2.5 | Are the stockpile of dusty materials covered by impervious sheeting or sprayed with water to maintain the entire surface wet or removed or backfilled within 24 hours of the excavation or unloading? | ✓ | | | |
| 2.6 | Are debris covered entirely by impervious sheeting, placed in an area sheltered on the top and 3 sides? | | ✓ | | |
| 2.7 | Is Ultra Low Sulphur Diesel used for all PME onsite? | ✓ | | | |
| 2.8 | Do the site vehicles use the wheel wash at the site exits? | ✓ | | | |
| 2.9 | Are materials transported on trucks covered? | | ✓ | | |
| 2.10 | Are all trucks loaded to a level within the side and tail boards? | | ✓ | | |
| 2.11 | Is all operation less than 6 minutes in any period of 4 hours or for less than 3 minutes continuously at any one time? | ✓ | | | |
| 2.12 | Is the unpaved road compacted regularly? | | ✓ | | |
| 2.13 | Is the road surface kept clear of loose materials? | | ✓ | | |
| 2.14 | Is the speed restricted for all vehicles moving within the site to minimize fugitive dust emission? | | ✓ | | |
| 2.15 | Are PME operated in a good manner and no black smoke emitted? (If yes, skip to part 3) | ✓ | | | |
| 2.16 | Are PME in operation not emitted for more than 6 minutes in any period of 4 hours or for more than 3 minutes continuously at any one time? | ✓ | | | |

**In-situ Provisioning of Proposed Extension of Academic Block,
The Swire Institute of Marine Science,
Faculty of Science, The University of Hong Kong,
Cape D'Aguilar Road, Shek O**

| | | N/A | Yes | No | Remarks |
|-------------------------|--|-----|-----|----|---------|
| 3. Water Quality | | | | | |
| 3.1 | Does the discharge licence obtain from EPD under WPCO by contractor? | ✓ | | | |
| 3.2 | Is the waste water prevented from entering the inland water and inshore water, and collected by licensed collector and discharged off site? | ✓ | | | |
| 3.3 | Is the surface run-off from construction site treated via adequately designed sand/silt removal facilities such as sand traps, silt traps and sedimentation tank | ✓ | | | |
| 3.4 | Is the STP first to prevent sewage from entering the inland water and inshore water, and then collected by licensed collector and discharged off site? | ✓ | | | |
| 3.5 | Is the vehicle washing bay located on a paved area and away from the sensitive receivers? | ✓ | | | |
| 3.6 | Is the contractor provide with a suitable backfill to prevent the site run-off from entering the public roads | ✓ | | | |
| 3.7 | Is that all water used on site re-circulated and re-used as dust suppression, wheel washing and general cleaning? | ✓ | | | |
| 3.8 | Are the online standby water sump pumps of sufficient capacity and with automatic devices provided on site? | ✓ | | | |
| 3.9 | Are the open stockpiles of construction materials on site or exposed earth surface avoided as far as practicable?(If no, answer 3.11) | | ✓ | | |
| 3.10 | Are the open stockpiles covered with impervious sheet such as tarpaulin sheet or similar fabric during rainstorms? | ✓ | | | |
| 3.11 | Is the site clear from stagnant water? | | ✓ | | |

**In-situ Provisioning of Proposed Extension of Academic Block,
The Swire Institute of Marine Science,
Faculty of Science, The University of Hong Kong,
Cape D'Aguilar Road, Shek O**

| | | N/A | Yes | No | Remarks |
|----------------------------|--|-----|-----|----|---------------------|
| 3.12 | Are the extra pumps used to pump the water into sedimentation tank during rainy days? | ✓ | | | |
| 3.13 | Is the Earth bund or sand bag barriers provided onsite to properly direct storm water to the silt removal facilities? | ✓ | | | |
| 3.14 | Is the construction sites cleaned on a regular basis? | | ✓ | | observation (1) (3) |
| 3.15 | Are the good site practices adopted to remove rubbish and litter from construction site | | ✓ | | |
| 3.16 | Are there sufficient chemical toilets provided in the works area? | | ✓ | | |
| 3.17 | Is a licensed waste collector deployed to clean the chemical toilets on a regular basis? | ✓ | | | |
| 3.18 | Are there notices posted at conspicuous locations to remind the workers not to discharge any sewage or sewage into the nearby environment? | | ✓ | | |
| 3.19 | Does the contractor include the sewage control measures during their onsite toolbox talk to increase the awareness of all workers? | | ✓ | | |
| 4. Waste Management | | | | | |
| 4.1 | Did the construction works carefully plan to minimize the amount of wastes generated and avoid unnecessary generation of wastes? | | ✓ | | |
| 4.2 | Are the sufficient waste disposal points and regular collection of wastes provided? | | ✓ | | |
| 4.3 | Does the contractor segregate and store different types of waste properly? | | ✓ | | |
| 4.4 | Are the dump trucks covered properly with impervious sheeting when leaving the site? | | ✓ | | |
| 4.5 | Do the Contractor register as a Chemical Waste Producer? | ✓ | | | |

**In-situ Provisioning of Proposed Extension of Academic Block,
The Swire Institute of Marine Science,
Faculty of Science, The University of Hong Kong,
Cape D'Aguilar Road, Shek O**




| | | N/A | Yes | No | Remarks |
|-------------------|--|-----|-----|----|---------|
| 4.6 | Do all chemical waste properly handled, stored, labeled, packaged and collected in accordance with the requirements of the Waste Disposal (Chemical Waste) (General) Regulation? | ✓ | | | |
| 4.7 | Do all C&D wastes be transported to the designated disposal facilities managed by CEDD and EPD? | | ✓ | | |
| 4.8 | Did the contractor prepare Waste Management Plan? | | ✓ | | |
| 4.9 | Did the toolbox talks include the specific topics? | | ✓ | | |
| 5. Ecology | | | | | |
| 5.1 | Is the access route and placement of equipment and stockpile in work area selected at existing developed area and disturbed land to minimize disturbance on vegetation? | | ✓ | | |
| 5.2 | Is the chosen temporary storage or stockpiling area and access routes far away from any identified plant species of conservation importance? | | ✓ | | |
| 5.3 | Are the construction activities restricted to the clearly defined works area? | | ✓ | | |
| 5.4 | Are the temporary works area reinstated immediately after completion of the construction works? | ✓ | | | |
| 5.5 | Are the disposal and treatment of waste carried out in a timely and proper manner | | ✓ | | |
| 5.6 | Are the open fires strictly prohibited to prevent any risk of wildfire? | | ✓ | | |
| 5.7 | Are the firefighting equipments prohibited in the works area before the commencement of works? | | ✓ | | |
| 5.8 | Is there proper implementation of the mitigation measures ensured by the resident site personnel? | | ✓ | | |

**In-situ Provisioning of Proposed Extension of Academic Block,
The Swire Institute of Marine Science,
Faculty of Science, The University of Hong Kong,
Cape D'Aguilar Road, Shek O**

| | | N/A | Yes | No | Remarks |
|--------------------------------|---|-----|-----|----|---------|
| 5.9 | Do the peripheral plant individuals have a setback of at least 1.5m in the protection zones? | | ✓ | | |
| 5.10 | Are the protection zones set up by contractor to fence off 6 plant species during construction with orange nets of at least 1m in height? | | ✓ | | |
| 6. Landscape and Visual | | | | | |
| 6.1 | Do LR1,LR2,LCA1 and LCA2 compensated with planting of native trees and shrubs? | ✓ | | | |
| 6.2 | Do LR1,LR2,LCA1 and LCA2 designed with minimum vegetation clearance? | | ✓ | | |
| 6.3 | Do LR1,LR2,LCA1 and LCA2 retain and preserve all plant species of conservation importance on site? | | ✓ | | |
| 6.4 | Do LR3 improve its amenity value by compensatory planting and natural regeneration of plants | ✓ | | | |
| 6.5 | Do VSR1,VSR2 and VSR3 erect hoarding with colour compatible to the surrounding around works area? | ✓ | | | |
| 7. Cultural Heritage | | | | | |
| 7.1 | Is the no-entry zone at the Cape D' Aguilar Lighthouse not fenced off by eye-catching orange net? | | ✓ | | |
| 7.2 | Is the road section close to the Lighthouse clear? | | ✓ | | |
| 7.3 | Is there no excavator used at the road section close to the Lighthouse? | ✓ | | | |
| 7.4 | Is the manual gear used for trenching work near the Lighthouse? | ✓ | | | |
| 7.5 | Do they monitor the vibration near the Lighthouse? | ✓ | | | |
| 8. Others | | | | | |
| 8.1 | Are the mitigation measures properly implement in general? | | ✓ | | |



**In-situ Provisioning of Proposed Extension of Academic Block,
The Swire Institute of Marine Science,
Faculty of Science, The University of Hong Kong,
Cape D'Aguilar Road, Shek O**

| | | |
|--|--|--|
| Observation: | | |
| <p>① Broken Concretes from^{found} the facade of of the building was found, clean-up shall be carried out</p> <p>② Noise curtain was spotted which might affect the noise reduction ^{Gap between} effectiveness effectiveness.</p> <p>③ Waste was found inside orange net on Site C.</p> | | |
| Signatures: | | |
| IEC's Representative/ Designated Staff | Main Contractor's Representative/ Designated Staff | Architect's Representative/ Designated Staff |
|  (Name: Nelson Tsui) |  (Name: Wong Kwok Guan) |  (Name: Ip Wai Ho) |
