MTR Corporation Limited

Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works

Monthly EM&A Report

(May 2023)

Verified by: ______ James Choi

Position: Independent Environmental Checker

Date: 8 June 2023

MTR Corporation Limited

Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works

Monthly EM&A Report

(May 2023)

Certified by:	Edan Li	4 den
y		\mathcal{O}

Position: Environmental Team Leader

Date: _____8 June 2023



MTR Corporation Limited

Consultancy Agreement No. NEX/1062

Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works – Advance Construction Works

Monthly EM&A Report No. 18

[Period from 1 to 31 May 2023]

	Name	Signature
Prepared & Checked:	Ho Pui Yin Kevin	Kn
Reviewed & Approved:	Angela Tong	Angel

 Version:
 A
 Date:
 7 June 2023

 This Monthly EM&A Report is prepared for MTR Corporation Limited and is given for its sole benefit in relation to and pursuant to Consultancy Agreement No. NEX/1062 and may not be disclosed to, quoted to or relied upon by any person other than MTR Corporation Limited without our prior written consent. No person (other than MTR Corporation Limited) into whose possession a copy of this report comes may rely on this plan without our express written consent and MTR

Corporation Limited may not rely on it for any purpose other than as described above.

AECOM Asia Co. Ltd. 8/F, Grand Central Plaza, Tower 2, 138 Shatin Rural Committee Road, Shatin, NT, Hong Kong Tel: (852) 3922 9000 Fax: (852) 3922 9797 www.aecom.com

Table of Contents

Pad	е

1	INTR	ODUCTION	.2
	1.1 1.2 1.3	Background Project Programme Purpose of the Report	
2		RONMENTAL MONITORING AND AUDIT	
	2.1	EM&A Results	3
3	IMPL	EMENTATION STATUS ON THE ENVIRONMENTAL PROTECTION REQUIREMENT	S 5

List of Tables

Table 1.1	Summary of Awarded Works Contracts
Table 2.1	Summary of Major Construction Activities in the Reporting Period
Table 2.2	Summary of 1-Hour TSP Monitoring Results in the Reporting Period
Table 2.3	Log for Environmental Complaints, Notification of Summons and Successful
	Prosecutions for the Reporting Month
Table 3.1	Summary of EP Submissions Status
	Log for Environmental Complaints, Notification of Summons and Successful Prosecutions for the Reporting Month

List of Appendices

- Appendix A Monthly EM&A Report for May 2023 Trial Piles And Site Formation for Siu Ho Wan Depot Property Development – Phase 1 Contract 1731
- Appendix B Monthly EM&A Report for May 2023 Cable Bridges and Associated Civil Works for Cable Diversion Works Contract 1732
- Appendix C Monthly EM&A Report for May 2023 Vehicular Access Bridge, Demolition of Paint Shop and Construction of EV Stabling Tracks Works Contract 1733

1 INTRODUCTION

1.1 Background

- 1.1.1 MTR Corporation Limited (MTRCL) had commenced a study to formulate a technically feasible development scheme for the Proposed Comprehensive Residential and Commercial Development atop Siu Ho Wan Depot (hereinafter referred to the "Oyster Bay (OYB) Property Development") to optimize housing supply. To facilitate the construction of the OYB Property Development, railway related works would be required. The existing Siu Ho Wan Depot (SHD) will undergo replanning works to make room for the phased construction of the OYB Property Development, while maintenance and supporting services to the existing Tung Chung Line (TCL), Airport Express Line (AEL) and Disneyland Resort Line (DRL) should be maintained without causing disruption to the normal operation. A new Oyster Bay (OYB) Station (formerly named as Siu Ho Wan Station (SHO)) has also been proposed along the TCL tracks to meet transport needs of the OYB Property Development and enable building of a sustainable community.
- 1.1.2 The Environmental Impact Assessment (EIA) Report (Register No.: AEIAR-214/2017) for the SHO and SHD Replanning Works (hereafter referred to as the "Project") was approved on 29 November 2017 under the Environmental Impact Assessment Ordinance (EIAO). Following the approval of the EIA Report, an Environmental Permit (EP) was granted on 22 March 2021 (EP No: EP-588/2021) for the construction and operation of the Project.

1.2 Project Programme

1.2.1 Three civil construction works contracts of the Project have been awarded since December 2021. The construction of the Project commenced in December 2021 and is expected to complete in 2023. **Table 1.1** summarises the information of the awarded Works Contracts.

	le 1.1 Summary of Awarded works contracts				
Works Contract	Description	Construction Start Date	Contractor	Environmental Team	
1731	Trial Piles and Site Formation for Siu Ho Wan Depot Property Development – Phase 1	January 2023	Gammon Construction Ltd.	WSP (Asia) Ltd.	
1732	Cable bridges and associated civil works for cable diversion	December 2021	Paul Y – CRCCI JV	Acuity Sustainability Consulting Ltd.	
1733	Vehicular Access Bridge, Demolition of Paint Shop and Construction of EV Stabling Tracks	April 2022	Build King Civil Engineering Ltd.	SGS Hong Kong Ltd.	

Table 1.1 Summary of Awarded Works Contracts

1.3 Purpose of the Report

1.3.1 The Environmental Monitoring and Audit (EM&A) programme for the Project commenced in December 2021. This is the seventeenth EM&A Report for the Project which summarises the EM&A works undertaken by the respective Contractor's ETs during the period from 1 to 31 May 2023.

2 ENVIRONMENTAL MONITORING AND AUDIT

2.1 EM&A Results

- 2.1.1 The EM&A Report for Works Contract 1731, 1732 and 1733 prepared by the Contractor's ET are provided in **Appendices A** to **C**. The EM&A Report provides details of the project information, EM&A requirements, impact monitoring and audit results for the Contract.
- 2.1.2 A summary of the major construction activities undertaken by the Contractor of Works Contract during the reporting period is presented in **Table 2.1**.

Table 2.1	Summary of Major Construction Activities in the Reporting Period		
Works Contract	Site	Construction Activities	
1731	Overall	Site Clearance & HoardingPre-drilling Works	
1732	Overall	 General survey works Instrumentation monitoring AB11 modification works Cable brackets construction along trackside Pier and truss installation for the cable bridges (Mainly post erection closure work, openings on the piers, E&M works in the bridge) Draw pits, ducting and cable trough installation 	
1733	Overall	 Excavation Substructure UU Diversion EV Tracks - Formation and Track installation Construction of southern ramp of vehicular access bridge Grout curtain works Chain Link Fence works 	

2.1.3 During the reporting period, impact monitoring for air quality was conducted in accordance with the EM&A Manual. No exceedances of the Action / Limit Level of 1-hour TSP due to the Project construction were recorded. Results of air quality is summarised in **Tables 2.2**. Details of the monitoring requirements, locations, equipment and methodology are presented in **Appendices A to C** of this Report.

|--|

Monitoring Station ID	Location	TSP Concentration (µg/m³)	Action Level (μg/m³)	Limit Level (µg/m³)	Exceedance due to the Project Construction (Yes/No)	
Works Contrac	Works Contract 1731, 1732 & 1733					
DM1	Siu Ho Wan Government Maintenance Depot	58.9 – 63.3	294.7	500	No	

2.1.4 No environmental complaints, notification of summons and successful prosecutions were recorded in the reporting period. Log for environmental complaints, notification of summons and successful prosecutions is provided in **Table 2.3**.

Table 2.3Log for Environmental Complaints, Notification of Summons and
Successful Prosecutions for the Reporting Month

Works Contract	Environmental Complaints	Notification of Summons	Successful Prosecutions
1731	0	0	0
1732	0	0	0
1733	0	0	0

2.1.5 Regular site inspections were conducted by the Contractor's ET on a weekly basis to check the implementation of environmental pollution control and mitigation measures for the Project. No non-conformance was identified in the reporting period.

3 IMPLEMENTATION STATUS ON THE ENVIRONMENTAL PROTECTION REQUIREMENTS

3.1.1 The Contractor has implemented all mitigation measures and requirements as stated in the EIA Report, EM&A Manual and EP (EP No: EP-588/2021). The status of required submissions under the EP as of the reporting period are summarised in **Table 3.1**.

EP Condition (EP-588/2021)	Submission	Submission date
Condition 1.12	Commencement Date of Construction	11 Jun 2021 (1 st submission) 12 Jul 2021 (2 nd submission) 12 Aug 2021 (3 rd submission)
Condition 2.7	Construction Works Phasing Schedule Proposal	1 Nov 2021 (1 st Submission) 20 Dec 2021 (2 nd Submission) 29 Dec 2021 (Deposited)
Condition 2.8	Environmental Permit Submission Schedule	12 Aug 2021 10 Sep 2021 (Deposited)
Condition 2.9	Management Organization	1 Nov 2021 (1 st Submission) 20 Dec 2021 (2 nd Submission) 21 Mar 2022 (3 rd Submission) 9 Aug 2022 (4 th Submission) 16 Nov 2022 (5 th Submission)
Condition 2.10	Construction Noise Mitigation Plan	1 Nov 2021 (1 st Submission) 20 Dec 2021 (2 nd Submission) 28 Dec 2021 (Deposited) 30 Dec 2022 (1 st Submission which covered Phase 1 main works) 29 Mar 2023 (2nd Submission which covered Phase 1 main works) 18 May 2023 (3rd Submission which covered Phase 1 main works)
Condition 2.11	Noise Mitigation Plan	31 Mar 2023 (1 st submission)
Condition 2.13	Waste Management Plan	1 Nov 2021 (1 st Submission) 20 Dec 2021 (2 nd Submission) 28 Dec 2021 (Deposited)
Condition 2.15	Landscape and Visual Plan(s)	27 Apr 2023 (1st submission)
Condition 3.3	Baseline Monitoring Report	1 Nov 2021 16 Nov 2021 (Deposited)
Condition 3.4	Monthly EM&A Report No.16 (Mar 2023)	To be submitted within 10 working days after the end of the reporting month
Condition 4.2	Dedicated Internet Website	12 Jan 2022

 Table 3.1
 Summary of EP Submissions Status

Appendix A

Monthly EM&A Report for May 2023 – Trial Piles and Site Formation for Siu Ho Wan Depot Property Development – Phase 1 Contract 1731 GAMMON CONSTRUCTION LIMITED

CONTRACT NO. 1731 TRIAL PILES AND SITE FORMATION FOR SIU HO WAN DEPOT PROPERTY DEVELOPMENT – PHASE 1

MONTHLY EM&A REPORT (MAY 2023)

JUNE 05, 2023

CONFIDENTIAL





Contract No. 1731 Trial Piles and Site Formation for Siu Ho Wan Depot Property Development – Phase 1

Monthly EM&A Report (MAY 2023)

FIRST ISSUE CONFIDENTIAL

PROJECT NO.: 2535700A DATE: JUNE 05, 2023

WSP 7/F ONE KOWLOON 1 WANG YUEN STREET KOWLOON BAY, HONG KONG

PHONE: +852 2579-8899 FAX: +852 2856-9902 WSP.COM

QUALITY MANAGEMENT

ISSUE/REVISION	FIRST ISSUE	REVISION 1	REVISION 2	REVISION 3
Remarks				
Date	5 June 2023			
Prepared by	Gloria Chow			
Signature	No			
Checked by	Dr Alex Cheung			
Signature	Cherry			
Authorised by	Dr Paul Kau			
Signature	Rle.			
Project number	2535700A			
File reference				

CONTRACT NO. 1731 TRIAL PILES AND SITE FORMATION FOR SIU HO WAN DEPOT PROPERTY DEVELOPMENT – PHASE 1

SIGNATURES

PREPARED BY

Gloria Chow Site Auditor

REVIEWED BY

Dr. Alex Cheung Environmental Team Leader

This report was prepared by WSP (Asia) for the account of Gammon Construction Limited, in accordance with the professional services agreement. The disclosure of any information contained in this report is the sole responsibility of the intended recipient. The material in it reflects WSP (Asia) Limited 's best judgement in light of the information available to it at the time of preparation. Any use which a third party makes of this report, or any reliance on or decisions to be made based on it, are the responsibility of such third parties. WSP (Asia) Limited accepts no responsibility for damages, if any, suffered by any third party as a result of decisions made or actions based on this report. This limitations statement is considered part of this report.

The original of the technology-based document sent herewith has been authenticated and will be retained by WSP for a minimum of ten years. Since the file transmitted is now out of WSP's control and its integrity can no longer be ensured, no guarantee may be given to by any modifications to be made to this document.

CONTRACT NO. 1731 TRIAL PILES AND SITE FORMATION FOR SIU HO WAN DEPOT PROPERTY DEVELOPMENT – PHASE 1

WSP MAY 2023 PAGE iv

vsp

TABLE OF CONTENTS

EXECUTIVE SUMMARY

1	INTRODUCTION	2
2	ENVIRONMENTAL MONITORING AND AUDIT	3
3	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS	7
4	EM&A SITE INSPECTION	8
5	FUTURE KEY ISSUES	9
6	CONCLUSION AND RECOMMENDATIONS	.10

Executive Summary

This Environmental Monitoring and Audit (EM&A) report presented the EM&A works carried out during the reporting period from 1 to 31 May 2023.

A summary of the construction works reported by the Main Contractor for the Project during the reporting month is listed below.

- Site Clearance & Hoarding
- Pre-drilling Works

A summary of regular construction dust monitoring activities in this reporting period is listed below:

Construction dust (1-hour TSP) monitoring	
DM1	15 times

Site inspections were conducted on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. Five (5) site inspections were conducted on 2, 8, 15, 22 and 29 May 2023 for this reporting period. One joint inspection with IEC was also conducted on 8 May 2023. The environmental performance of the Project was considered satisfactory.

Details of waste management can be referred to Section 2.4.

No Action or Limit Levels exceedance of 1-hour TSP was recorded during this reporting period.

No complaints, notification of summons and prosecutions received during May 2023. Statistics on complaints, notifications of summons and successful prosecutions are presented in **Section 3**.

No changes of EM&A programme were made in this reporting period.

A summary of works to be conducted in the coming reporting months is listed below.

- Site Clearance & Hoarding
- Pre-drilling Works
- Bored Piling Works

1 INTRODUCTION

1.1 BACKGROUND

- 1.1.1 The "Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works" (EP-588/2021) project includes:
 - Siu Ho Wan Depot (SHD) replanning works, within the existing SHD boundary including construction of concrete slab over the SHD to provide support for future SHD Topside Development;
 - Construction of the new Oyster Bay (OYB) Station (formerly named as Siu Ho Wan Station (SHO)) and modification of the associated trackworks of the existing Airport Express Line/Tung Chung Line; and
 - Construction of other supporting facilities including the western access, the local accesses and sewerage network outside existing SHD boundary.
- 1.1.2 The "Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works" Impact Assessment Report (Register No. AEIAR-214/2017) was approved by the Environmental Protection Department (EPD) with conditions on 29 November 2017. The latest Environmental Permit (No. EP-588/2021) was issued by the EPD on 22 March 2021.
- 1.1.3 WSP (Asia) Ltd. (WSP) is commissioned by Gammon Construction Limited to provide Environmental Team (ET) services during the construction phase of Contract No. 1731 Trial Piles and Site Formation for Siu Ho Wan Depot Property Development – Phase 1 (hereafter as "the Project").

1.2 PROJECT PROGRAMME

- 1.2.1 A summary of the construction works reported by the Main Contractor for the Project during the reporting month is listed below.
 - (1) Site Clearance & Hoarding
 - (2) Pre-drilling Works
- 1.2.2 The construction programme is provided in **Appendix A**.

1.3 PURPOSE OF THE REPORT

1.3.1 This is the 5th monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A works carried out during the reporting period from 1 to 31 May 2023.

2 ENVIRONMENTAL MONITORING AND AUDIT

2.1 SUMMARY OF ENVIRONMENTAL LICENSE, NOTIFICATION, PERMIT AND DOCUMENTATIONS

2.1.1 A summary of valid permits, licenses, and notifications on environmental protection for this Project are listed in **Table 2.1**.

Table 2.1	Summary of the Status of Valid Environmental License, Notification, Permit and
	Documentation

Permit / Licenses / Valid Notification /		Period	Status	Remark	
Reference No.	From	То	Status	Remark	
Environmental Permit					
EP-588/2021	22 Mar 2021	N/A	Valid		
Billing Account under	Waste Dispos	al (Charges fo	r Disposal	of Construction Waste)	
Regulation					
7045243	6 Oct 2022	N/A	Valid		
Construction Noise P	ermit				
GW-RS1030-22	6 Dec 2022	5 Jun 2023	Expired	Valid until 11 May 2023	
GW-RS0318-23	11 May 2023	10 Nov 2023	Expired	Valid until 29 May 2023	
GW-RS0397-23	29 May 2023	28 Nov 2023	Valid		
Notification Pursuant to Section 3(1) of the Air Pollution Control (Construction Dust)					
Regulation					
483822	N/A	N/A	Notified	Notification submitted	
403022	IN/A	IN/A	Notified	on 2 Sep 2022	
Register of Chemical	Waste Produce	er			
5213-961-G2980-01	7 Oct 2022	N/A	Valid		
Water Pollution Disch	arge License				
WT000463109-2023	22 Feb 2023	29 Feb 2028	Valid		

2.2 ENVIRONMENTAL STATUS

2.2.1 Environment Permit (EP) conditions under the Environmental Impact Assessment Ordinance (EIAO), submission status the EP and implementation status of mitigation measures had been reviewed and implemented on schedule. The status of required submissions under the EP (No. EP-588/2021) as of the reporting period for the Project are summarised in **Table 2.2**.

Table 2.2	Summary of Status of Required Submission for EP-588/2021 for the Project
-----------	--

EP Condition	Submission	Submission Date
(EP-588/2021)		
Condition 1.12	Commencement Date of Construction	11 Jun 2021 (1 st submission)

		12 Jul 2021 (2 nd submission)
		12 Aug 2021 (3 rd submission)
	Construction Works Phasing Schedule	1 Nov 2021 (1 st Submission)
Condition 2.7	Proposal	20 Dec 2021 (2 nd Submission)
		29 Dec 2021 (Deposited)
Condition 2.8	Environmental Permit Submission	12 Aug 2021
	Schedule	10 Sep 2021 (Deposited)
		1 Nov 2021 (1 st Submission)
		20 Dec 2021 (2 nd Submission)
Condition 2.9	Management Organization	21 Mar 2022 (3 rd Submission)
		9 Aug 2022 (4 th Submission)
		16 Nov 2022 (5 th Submission)
		1 Nov 2021 (1 st Submission)
		20 Dec 2021 (2 nd Submission)
		28 Dec 2021 (Deposited)
		30 Dec 2022 (1 st Submission
Condition 2.10	Construction Noise Mitigation Plan	which covered Phase 1 main
		works)
		29 Mar 2023 (2 nd Submission
		which covered Phase 1 main
		works) 18 May 2023 (3 rd Submission)
Condition 2.11	Noise Mitigation Plan	31 Mar 2023 (1 st Submission)
Condition 2.11		1 Nov 2021 (1 st Submission)
Condition 2.13	Waste Management Plan	20 Dec 2021 (2^{nd} Submission)
Condition 2.13	Waste Management Flan	28 Dec 2021 (Deposited)
Condition 2.15	Landscape & Visual Plan	27 April 2023 (1 st Submission)
00110110112.13		1 Nov 2021
Condition 3.3	Baseline Monitoring Report	16 Nov 2021 (Deposited)
Condition 3.4	Monthly EM&A Report (Jan 2023)	13 Feb 2023
Condition 3.4	Monthly EM&A Report (Feb 2023)	10 Mar 2023
Condition 3.4	Monthly EM&A Report (Mar 2023)	17 April 2023
Condition 3.4	Monthly EM&A Report (Apr 2023)	9 May 2023
		To be submitted within 10
Condition 3.4	Monthly EM&A Report (May 2023)	working days after the end of
		the reporting month
Condition 4.2	Dedicated Internet Website	12 Jan 2022
1	1	1

2.3 AIR QUALITY

2.3.1 Impact monitoring had been carried out in accordance with Section 2.6 of the approved EM&A Manual, with sampling frequency of at least 3 times in every 5 days undertaken, to determine the 1-hour total suspended particulates (TSP) levels at the monitoring location during this reporting period.

- 2.3.2 General meteorological conditions (wind speed, direction and precipitation) and notes regarding any significant adjacent dust producing sources had also been recorded throughout the impact monitoring period.
- 2.3.3 Portable direct reading dust meter was used to carry out the 1-hour TSP monitoring. Portable direction reading dust meters used for the monitoring were proven to IEC to be capable of achieving comparable result as that of the HVS and thus were used for sampling.
- 2.3.4 The portable direct reading dust meters used for the 1-hour TSP measurement during this reporting period are summarised in **Table 2.3**.

Measuring Monitoring		suring Monitoring Brand and Model		Date of	
Parameter	Equipment		Number	Calibration	
1-hour TSP	Portable direct reading dust meter (1-hour TSP)	Sibata Digital Dust Monitor (Model No. LD-3B)	A.005.16a	4 Apr 2023	

Table 2.3	Construction	Duct	Monitoring	Equipmont
Table 2.5	Construction	Dusi	wonitoring	Equipment

- 2.3.5 The portable direct reading dust meters were calibrated at a 1-year interval against a High-Volume Sampler, TE-5170. Calibration Certificates are provided in **Appendix D**.
- 2.3.6 The 1-hour TSP measurement followed manufacturer's instruction manual. Zeroing the portable direct reading meter was proceed prior to each measurement to ensure maximum accuracy of concentration measurements.
- 2.3.7 The 1-hour TSP was sampled by drawing air into the portable direct reading dust meter where particular concentrations were measured instantaneously with an in-built silicon detector sensing light scattered by the particulates in the sampled air. Continuous TSP levels were indicated and logged by a built-in data logger compatible with Windows based program to facilitate data collection, analysis and reporting.
- 2.3.8 Location of the designated dust monitoring station is described in **Table 2.4** and shown on **Appendix E**.

 Table 2.4
 Construction Dust Monitoring Location

Monitoring Station ID	Dust Monitoring Station
DM1	Siu Ho Wan Government Maintenance Depot

2.3.9 Dust impact monitoring was carried out on 4, 10, 16, 22 and 27 May 2023 during this reporting period. Schedule of the dust impact monitoring for this reporting period is provided in Appendix F. It is observed that major dust sources are from North Lantau Highway and Cheung Tung Road. Results for the 1-hour TSP are summarised in Table 2.5. Measurement data are shown in Appendix G.

Table 2.5 Summary of 1-hour TSP Monitoring Rest	able 2.5 Si	ary of 1-hour TSP Monitoring Re	sults
---	-------------	---------------------------------	-------

Monitoring Location	Range (µg/m³)	Action Level (μg/m³)	Limit Level (µg/m³)	No. of Exceedances
DM1	58.9 – 63.3	294.7	500.0	0

2.3.10 Schedule of the dust impact monitoring for next reporting period is provided in Appendix H.

2.4 WASTE MANAGEMENT

- 2.4.1 Waste generated from this Project includes inert C&D materials and non-inert C&D materials. Non-inert C&D would include, but not limited to general refuse, bamboo, timber, vegetation, paper and plastic that cannot be transported to public fill.
- 2.4.2 Quantities of different types of waste generated in this reporting month are summarised in **Table 2.6**. Details of cumulative waste management data are shown in **Appendix I**.

	Quantity											
			Non-inert C&D Materials									
Reporting	Inert C&D	Chemical	Others, i.e.	Recycled Materials								
period	Materials	Waste	General Refuse	Paper /	Plastics	Metals	Yard Waste					
	(tonnes)	(tonnes)	nnes) disposed at Car		(tonnes)	(tonnes)	(tonnes)					
			Landfill (tonnes)	(tonnes)	(10111185)	(tornes)	(torines)					
May 2023	40.34	0	1.66	0	0	0	0					

 Table 2.6
 Quantities of Waste Generated during this Reporting Period

- 2.4.3 All dump trucks for C&D materials transportation and disposal were equipped with Global Positioning System (GPS) for real time tracking and monitoring their travel routings and parking locations in order to avoid illegal dumping or landfilling of C&D materials.
- 2.4.4 The GPS data including travel routings of dump trucks was reviewed by the ET and IEC, and no illegal dumping activities were suspected.

3 SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS

- 3.1.1 The Environmental Complaint Handling Procedure is presented in Appendix J.
- 3.1.2 Should non-compliance of the air quality criteria occur, action in accordance with the Event and Action Plan in **Appendix K** shall be carried out.
- 3.1.3 No Action and Limit Levels exceedance of 1-hour TSP was recorded during this reporting period.
- 3.1.4 No complaints, notification of summons and prosecutions received during May 2023.
- 3.1.5 Statistics on complaints, notifications of summons and successful prosecutions are summarized in **Appendix L**.

EM&A SITE INSPECTION 4

4.1.1 Site inspections were conducted on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. Five (5) site inspections were conducted on 2, 8, 15, 22 and 29 May 2023 for this reporting period. One joint inspection with IEC was also conducted on 08 May 2023. Key observations during the site inspections are summarized in Table 4.1.

Table 4.1 S	ite Observations	
Date	Observation/ Recommendation	Follow-up Status
02 May 2023	Nil	Nil
08 May 2023	Nil	Nil
15 May 2023	Nil	Nil
22 May 2023	Nil	Nil
29 May 2023	Nil	Nil

4.1.2 The mitigation measures detailed in the EIA Study Report, Environmental Permit, contract documents and the EM&A Manual are implemented as much as practical during this reporting period. The Implementation Status of the Environmental Mitigation Measures (EMIS) is presented in Appendix M.

5 FUTURE KEY ISSUES

- 5.1.1 Works to be conducted in the coming reporting months are:
 - (1) Site Clearance and Hoarding
 - (2) Pre-drilling Works
 - (3) Bored Piling Works

6 CONCLUSION AND RECOMMENDATIONS


- 6.1.1 This monthly EM&A Report presented the EM&A works carried out during the reporting period from 1 to 31 May 2023.
- 6.1.2 Air quality impact monitoring was carried out during the report period. No exceedance of the Action and Limit Levels was recorded for air quality impact monitoring during this reporting period.
- 6.1.3 Five (5) weekly site inspections have been conducted during this reporting period. A joint site inspection with the IEC was conducted on 08 May 2023. Observations were reported in the weekly inspection checklists. The environmental performance of the Project was considered satisfactory.
- 6.1.4 No complaints, notification of summons and prosecutions received during this reporting period.
- 6.1.5 The proposed mitigation measures were properly implemented and were considered effective and efficient in pollution control.

Appendix A Construction Programme

Appendix 2.1 Construction Programme

Construction Activities		2021					2022					2023						2024											
		JF	MA	M	JJ	AS	6 0	N D	JF	M	A M	JJ	A	S 0	N D	JF	F M	A M	JJ	A	S 0	N [DJ	FN	1 A	M J	JA	SC	IND
Contract 1731 - Trail Pile for SHD Phase 1	1																												
Site Clearance & Hoarding	1.1																												
Bored Piling Works	1.3																												

Appendix B Project Organisation Chart

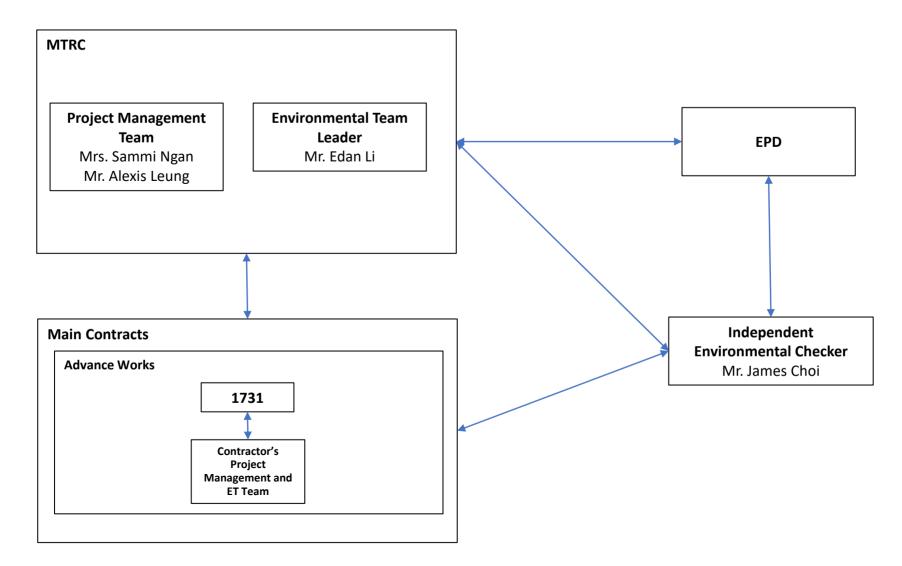

Legend:

Communication channel


MTRC - Project Management Team										
Position	Name	Telephone								
Chief Construction Manager - OYB	Mrs. Sammi Ngan	2208 3753								
Senior Construction Mananger - Civil	Mr. Alexis Leung	2208 3968								

MTRC - Environmental Team										
Position	Name	Telephone								
Environmental Team Leader	Mr. Edan Li	2688 1179								
Environmental Team Member	Mr. Cyrus Lau	2688 1585								

ANewR Consulting Limited - IEC										
Position	Name	Telephone								
Independent Environmental Checker	Mr. James Choi	2618 2836								

Main Works Contract	Description	Contractor	Position	Name	Telephone
	Trail piles and site formation for Siu Ho	Common	Senior Project Manager	Carl Chan	9275 9207
1731	Wan Depot Property Development -	Gammon Construction Ltd	Environmental Officer	Chris Tse	9127 7571
	Phase 1	Construction Ltu	Environmental Team Leader	Alex Cheung	9832 5750

Appendix C Location Plan

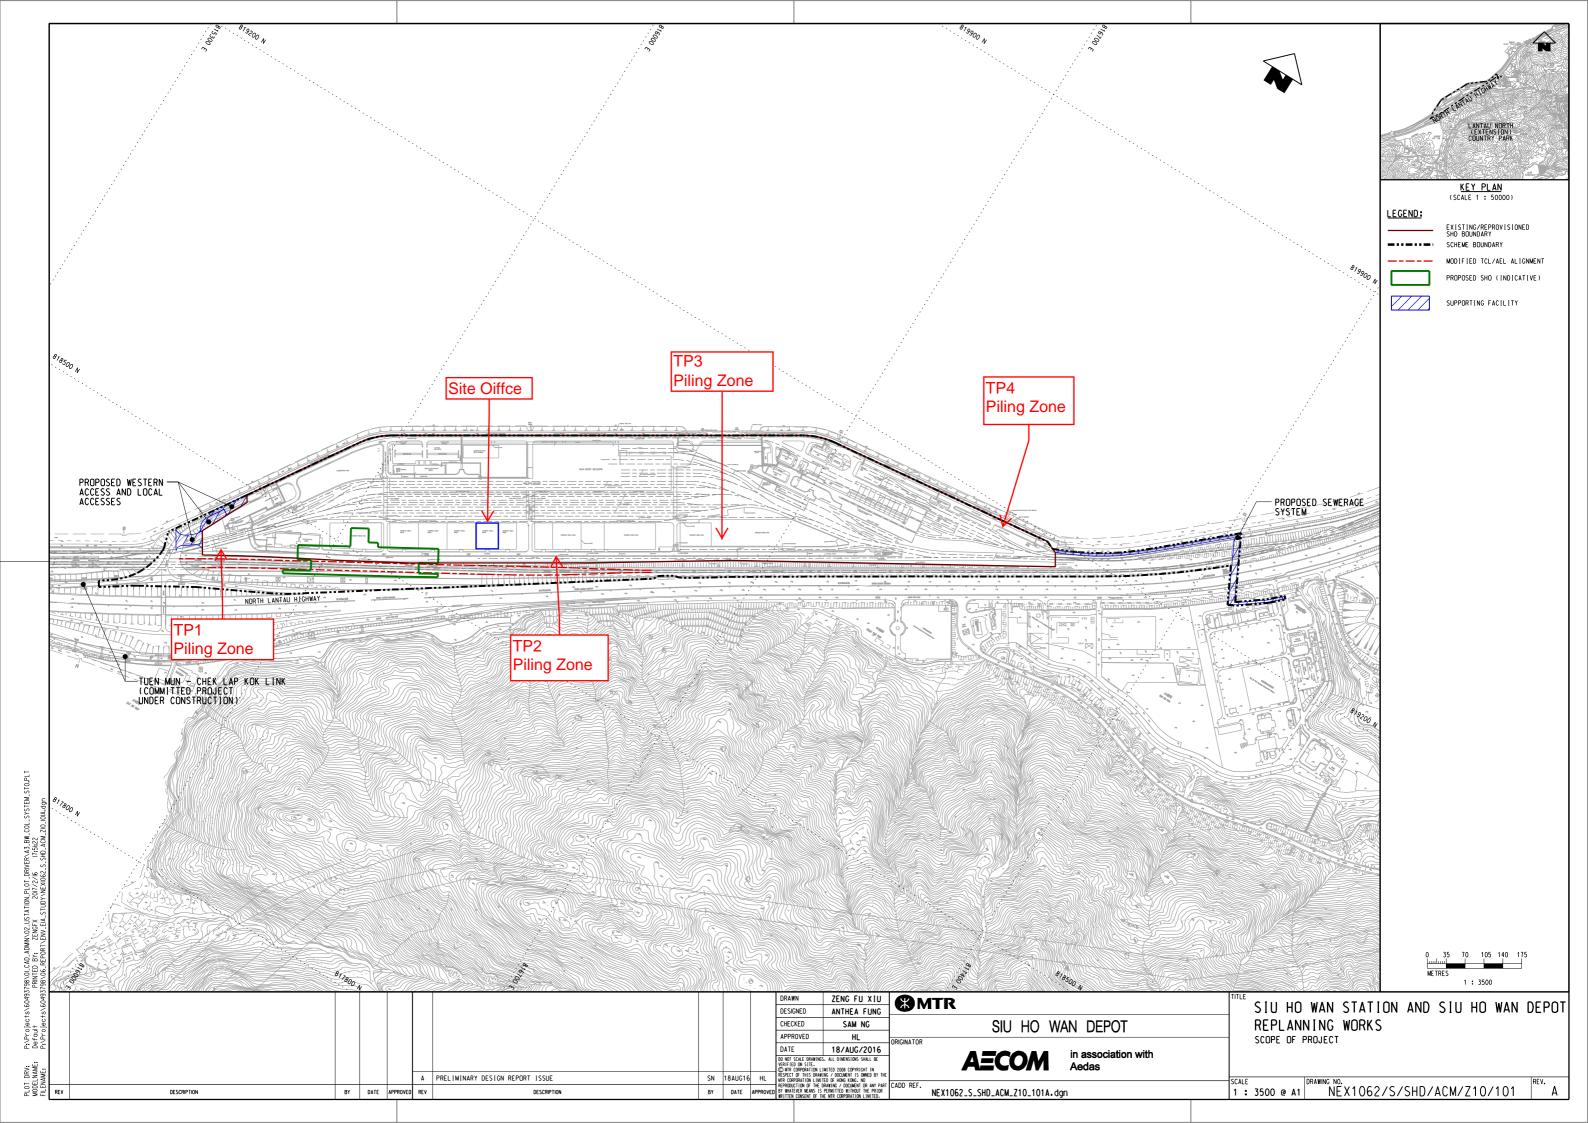


Appendix DCalibration Certification of Portable Direct
Reading Dust Meters

EQUIPMENT CALIBRATION RECORD

Type:			Laser Dus	t Monitor						
	urer/Brand:		SIBATA							
Model No			LD-3B							
Equipmen	t No.:		A.005.16a	a						
Sensitivity	Adjustment Sca	le Setting:	521 CPM							
Operator: WS CHAN										
Standard Equimment										
Standard	quimment									
Equipmen	t:		High Volu	me Samp	ler					
Venue:	-		Pedestria		-		•			
Model No	.:		TE-5170				•			
Serial No.:			10273							
Last Calibr	ation Date:		4-Apr-23							
Calibration	n Result									
•	Adjustment Sca	- ·		-		521	CPM			
Sensitivity	Adjustment Sca	le Setting (After	Calibratio	n):		521	CPM			
Haun	Dete	Time	Amelaiant	Condition	Concentration (1)	Total Count(2)	Count/			
Hour	Date	Time	Temp (°C)	Condition	-		Count/ Minute③			
	(dd/mm/yy)		remp (c)	R.H.(%)	(mg/m3) Y-axis		X-axis			
1	26/04/23	9:00-10:00	23.5	65	0.0490	1860	31.00			
2	26/04/23	10:00-11:00	23.5	65	0.0500	1940	32.33			
3	26/04/23	11:00-12:00	23.5	65	0.0520	2020	33.67			
4	26/04/23	12:00-13:00	23.5	65	0.0540	2150	35.83			
Note:		data was measu								
	<u> </u>	was logged by L			•					
		te was calculate))					
By Linear l	Regression of Y c	on X								
	Slope (K-factor)	:	0.0015							
	Correlation coe	fficient:	0.9997							
Validity of Calibration Record: 26-Apr-24										
Dowoorko										
Remarks:										

Appendix E Location Plan of Air Quality Monitoring Station

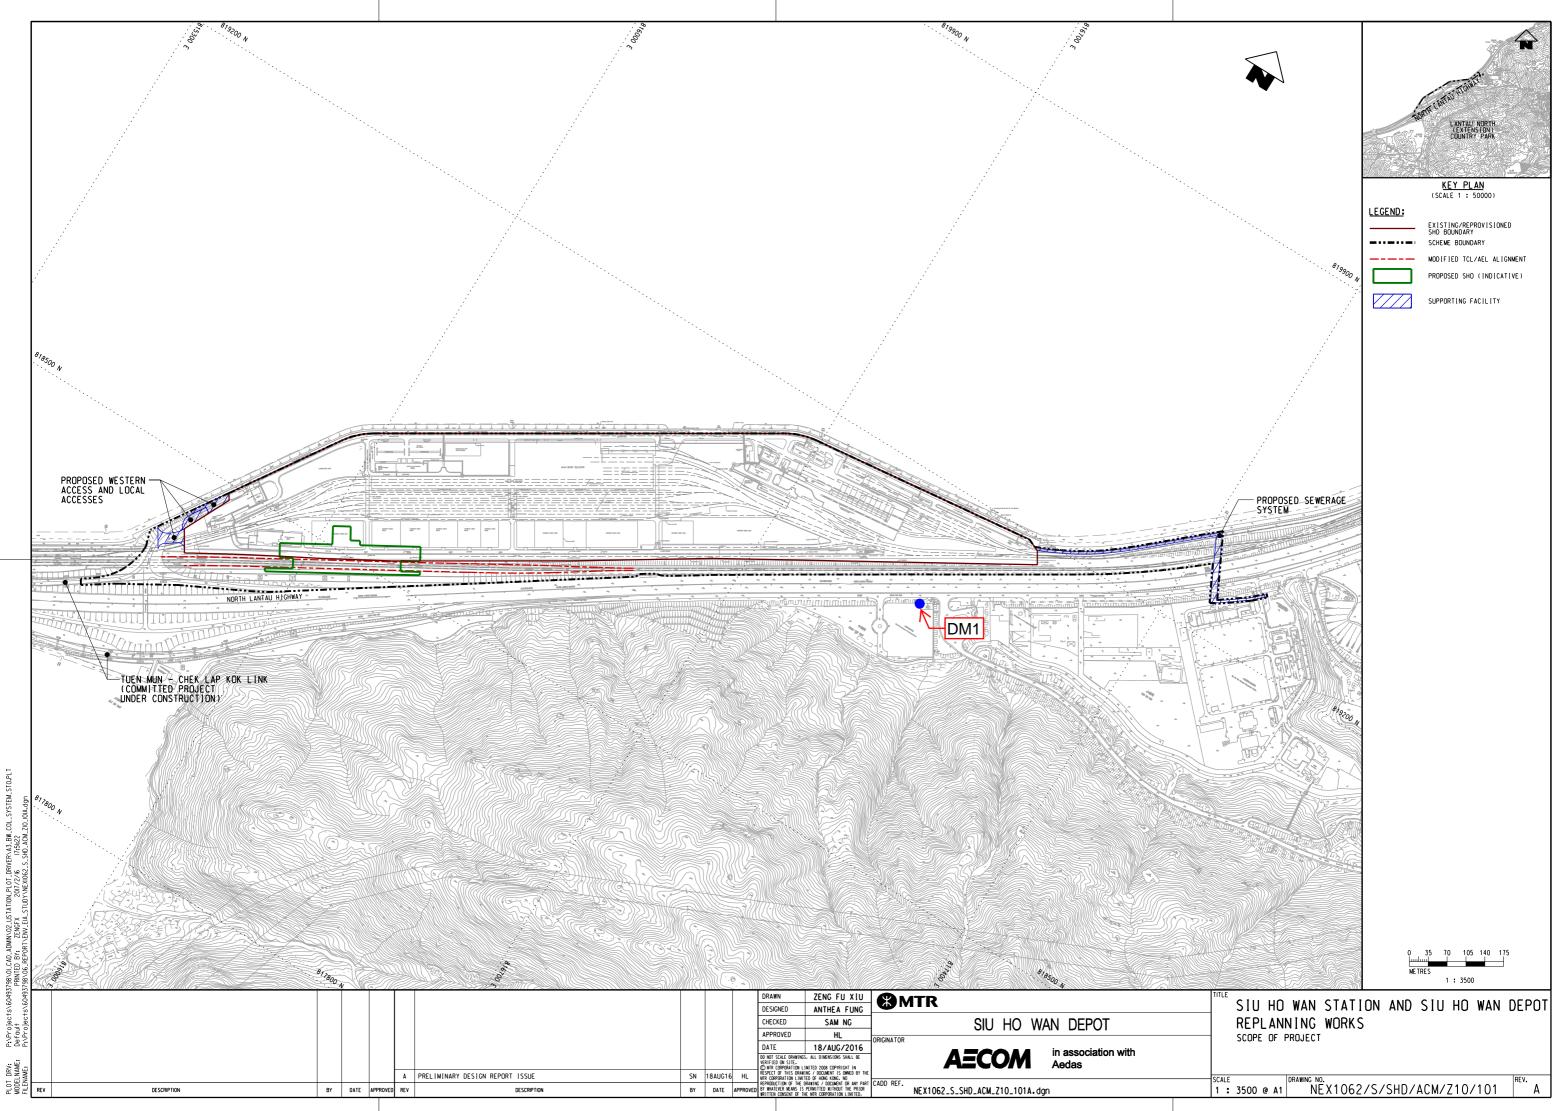

Appendix F Monitoring Schedule of This Reporting Period

Consultancy Agreement No.NEX/1062

Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works - Advance Constuction Works Dust and Noise Monitoring Schedule in May 2023

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-May	2-May	3-May	4-May	5-May	6-May
				1-hr Dust Monitoring		
7-May	8-May	9-May	10-May	11-May	12-May	13-May
			1-hr Dust Monitoring			
14-May	15-May	16-May	17-May	18-May	19-May	20-May
		1-hr Dust Monitoring				
21-May	22-May	23-May	24-May	25-May	26-May	27-May
	1-hr Dust Monitoring					1-hr Dust Monitoring
28-May	29-May	30-May	31-May			

Appendix G Air Quality Monitoring Data

Impact Air Quality Monitoring Results

	Start	1st Hour	2nd Hour	3rd Hour	Action Level	Limit Level	Exceedance
Data	Time (hh:mm)	Conc. (µg/m ³)	Conc. (µg/m³)	Conc. (µg/m³)	Conc. (µg/m³)	Conc. (µg/m³)	(Y/N)
Date	<u> </u>				(µg/iii)	(µg/m)	N
4-May-23	11:05	60.2	62.8	63.3			N
10-May-23	11:00	60.6	61.8	60.2			N
16-May-23	13:45	58.9	61.1	62.0	294.7	500.0	N
22-May-23	10:50	59.5	60.9	61.1			N
27-May-23	11:10	62.2	61.3	62.4			N
<u></u>			Average	61.2			
			Min	58.9			
			Max	63.3			

1-hour TSP Monitoring Results at Station - DM1 Siu Ho Wan Government Maintenance Depot

Appendix H Monitoring Schedule of Next Reporting Period

Consultancy Agreement No.NEX/1062

Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works - Advance Constuction Works Tentative Dust and Noise Monitoring Schedule in June 2023

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1-Jun	2-Jun	3-Jun
				1-hr Dust Monitoring		
4-Jun	5-Jun	6-Jun	7-Jun	8-Jun	9-Jun	10-Jun
			1-hr Dust Monitoring			
11-Jun	12-Jun	13-Jun	14-Jun	15-Jun	16-Jun	17-Jun
		1-hr Dust Monitoring				
18-Jun	19-Jun	20-Jun	21-Jun	22-Jun	23-Jun	24-Jun
	1-hr Dust Monitoring					1-hr Dust Monitoring
25-Jun	26-Jun	27-Jun	28-Jun	29-Jun	30-Jun	
					1-hr Dust Monitoring	

Remark: The monitoring schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather).

Appendix I Waste Flow Table


Monthly Summary Waste Flow Table

		Actual Quantities of Inert C&D Materials Generated						Actual (Quantities of Non-	inert C&D Materia	als Generated	
Month	(a) Total Quantity Generated	(b) Hard Rock and Large Broken Concrete	(c) Reused in the Contract	(d) Reused in other Projects	(e) Disposed of as Public Fill	(f) Imported Fill	(g) Metals	(h) Paper / cardboard packaging	(i) Plastics	(j) Chemical Waste	(k) Recyclable Yard Waste	(l) Others, i.e. General Refuse disposed of at Landfill
	(m^{3})	(m^{3})	(m^{3})	(m^{3})	(tonnes)	(m^{3})	(tonnes)	(tonnes)	(tonnes)	(tonnes)	(tonnes)	(tonnes)
Jan-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.78
Feb-23	0.00	0.00	0.00	0.00	3.17	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Mar-23	0.00	0.00	0.00	0.00	37.50	0.00	0.00	0.00	0.00	0.00	0.00	0.61
Apr-23	0.00	0.00	0.00	0.00	210.16	0.00	0.00	0.00	0.00	0.00	0.00	0.81
May-23	0.00	0.00	0.00	0.00	40.34	0.00	0.00	0.00	0.00	0.00	0.00	1.66
Total	0.00	0.00	0.00	0.00	291.17	0.00	0.00	0.00	0.00	0.00	0.00	4.86

Project: Contract No. 1731 Trial Piles and Site Formation for Siu Ho Wan Depot Property Development - Phase 1

Appendix J Complaint Handling Procedure

Complaint Handling Procedure

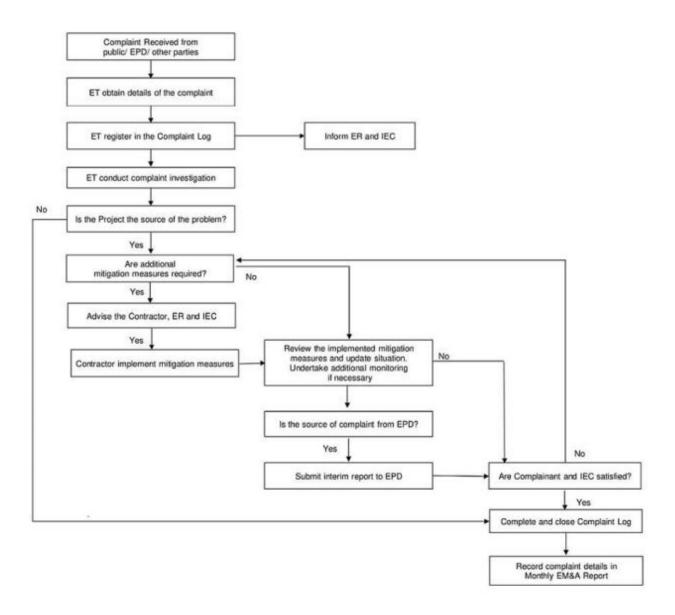

Appendix K Event and Action Plan for Air Quality Monitoring

	Action									
Event		Environmental Team	In	ndependent Environmental Checker	E	Engineer's Representative		CONTRACTOR		
ACTION LEVEL										
one sample	 1. 2. 3. 4. 	Repeat measurement to confirm findings; If exceedance is confirmed, inform the Contractor, IEC and ER; Identify source(s), investigate the causes of exceedance and propose remedial measures; and Increase monitoring frequency.	1. 2. 3. 4.	Check monitoring data submitted by the ET; Check Contractor's working method; Discuss with ET, ER and Contractor on possible remedial measures; and Review and advise the ET and ER on the effectiveness of the proposed remedial measures.	1.	Confirm receipt of notification of exceedance in writing.	1. 2. 3.	agreed with the ER as appropriate.		
Exceedance for two or more consecutive samples	 3. 4. 5. 6. 7. 	Repeat measurements to confirm findings; If exceedance is confirmed, informed Contractor, IEC and ER; Identify source(s), investigate the causes of exceedance and propose remedial measures; Increase monitoring frequency to daily; Advise the Contractor and ER on the effectiveness of the proposed remedial measures; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with Contractor, IEC and ER to discuss the remedial measures to be taken; and If exceedance stops, cease additional monitoring.	 1. 2. 3. 4. 5. 	Check monitoring data submitted by the ET; Check Contractor's working method; Discuss with ET, ER and Contractor on possible remedial measures; Review and advise the ET and ER on the effectiveness of the proposed remedial measures; and Supervise implementation of remedial measures.	1. 2. 3.	notification of exceedance in writing;	1. 2. 3. 4.	Identify source(s) and investigate the causes of exceedance; Submit proposals for remedial measures to the ER, ET and IEC within three working days of notification for agreement; Implement the agreed proposals; and Amend proposal as appropriate.		

		-	tion	
Event	Environmental Team	Independent Environmental Checker	Engineer's Representative	CONTRACTOR
LIMIT LEVEL				
Exceedance for one sample	 Repeat measurement to confirm findings; If exceedance is confirmed, inform the Contractor, IEC, EPD and ER; Identify source(s), investigate the causes of exceedance and propose remedial; Increase monitoring frequency to daily; and Discuss with the ER, IEC and Contractor on the remedial measures and assess effectiveness. 	 Check monitoring data submitted by the ET; Check Contractor's working method; Discuss with the ET, ER and Contractor on possible remedial measures; Review and advise the ET and ER on the effectiveness of the proposed remedial measures; and Supervise implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Review and agree on the remedial measures proposed by the Contractor; and Ensure remedial measures properly implemented. 	 Identify source(s) and investigate the causes of exceedance; Take immediate action to avoid further exceedance; Submit proposals for remedial measures to ER, ET and IEC within three working days of notification for agreement; Implement the agreed proposals; and Amend proposal if appropriate.
Exceedance for two or more consecutive samples	 Repeat measurement to confirm findings; If exceedance is confirmed, inform IEC, ER, Contractor and EPD; Identify source(s), investigate the causes of exceedance and propose remedial measures; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and If exceedance stops, cease additional monitoring. 	 Check monitoring data submitted by the ET; Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and Supervise the implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures; and If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Identity source(s) and investigate the causes of exceedance; Take immediate action to avoid further exceedance; Submit proposals for remedial measures to the ER, IEC and ET within three working days of notification for agreement; Implement the agreed proposals; Revise and resubmit proposals if problem still not under control; and Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Appendix L Statistics on Complaint, Notification of Summons and Successful Prosecution

Statistics on Complaints, Notification of Summons and Successful Prosecution

 Table F1
 Statistical Summary of Environmental Complaint

Deperting Deried	Enviror	Environmental Complaint Statistics					
Reporting Period	Frequency	Cumulative	Complaint Nature				
1 May 2023							
to	0	0	N/A				
31 May 2023							

 Table F2
 Statistical Summary of Environmental Non-compliance

Poparting Pariod	Environme	onmental Non-compliance Statistics					
Reporting Period	Frequency	Cumulative	Details				
1 May 2023							
to	0	0	N/A				
31 May 2023							

 Table F3
 Statistical Summary of Environmental Summons

Poparting Pariod	Enviror	Environmental Summons Statistics					
Reporting Period	Frequency	Cumulative	Details				
1 May 2023							
to	0	0	N/A				
31 May 2023							

 Table F4
 Statistical Summary of Environmental Prosecution

Departing Deried	Environ	mental Prosecution S	Statistics
Reporting Period	Frequency	Cumulative	Details
1 May 2023			
to	0	0	N/A
31 May 2023			

Appendix M Environmental Mitigation Implementation Schedule

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
Air Qual	ity (Construction Phase)						
S3.8.1	Watering once per hour on active works areas, exposed areas and unpaved haul roads during working hours.	To minimize dust impacts	Contractor	All works area	Construction phase	Air Pollution Control Ordinance (APCO)	Implemented
S3.8.9	 Implementation of dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices should be carried out to further minimize construction dust impact: Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. Use of frequent water for particularly dusty construction areas and areas close to ASRs. Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines. Open stockpiles should be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations. Establishment and use of vehicle wheel and body washing facilities at the exit points of the site. Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading 	To minimize dust impacts	Contractor	All works area	Construction phase	Air Pollution Control Ordinance (APCO)	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods. Imposition of speed controls for vehicles on unpaved site roads. 8 kilometres per hour is the recommended limit. Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs. Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides. Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed. Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system. 	Address					
	pact (Construction Phase)						
S4.5.16	 Implement the following good site practices as far as practicable: Only well-maintained plant should be operated on-site and plant should be 	To minimise impacts to surrounding habitats	Contractor	All works area	Construction phase	TM-EIAO	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 serviced regularly during the construction program. Silencers or mufflers on construction equipment should be utilised and should be properly maintained during the construction program. Mobile plant, is any, should be sited as far from NSRs as possible. Machine and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum. Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 						
S4.5.17	Adopting quiet PME is recommended. The type of quiet PME adopted in this assessment is for reference only. The contractors may adopt alternative quiet PME as long as it can be demonstrated that they would not result in construction noise impacts worse than those predicted in this assessment	To reduce impact to affected NSRs	Contractor	All works area	Construction phase	TM-EIAO	Implemented
S4.5.19	Use of noise barriers and noise enclosures to provide screening for construction plant where recommended.	To reduce impact to affected NSRs	Contractor	All works area	Construction phase	TM-EIAO	N/A
Water Qu	uality Impact (Construction Phase)						
S5.8.4	Surface and road run-off from construction sites should be discharged into storm drains via adequately	To minimise impact from	Contractor	All works area	Construction phase	Water Pollution Control	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	designed sand/silt removal facilities such as sand traps, silt traps and sedimentation basins. Channels or earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Perimeter channels should be provided on site boundaries where necessary to intercept storm run-off from outside the site so that it will not wash across the site. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.	construction site run-off				Ordinance (WPCO), Technical Memorandum on EIA Ordinance (EIAO-TM), ProPECC PN 1/94, Technical Memorandum on Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters (TM- DSS)	
S5.8.5	Silt removal facilities, channels and manholes should be maintained and the deposited silt and grit should be removed regularly, at the onset of and after each rainstorm to prevent local flooding. Any practical options for the diversion and re- alignment of drainage should comply with both engineering and environmental requirements in order to provide adequate hydraulic capacity of all drains.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented
S5.8.6	Construction works should be programmed to minimize soil excavation works in rainy seasons (April to September). If soil excavation cannot be avoided in these months or at any time of year when rainstorms are likely, for the purpose of preventing soil erosion,	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
05.0.7	temporary exposed slope surfaces should be covered e.g. by tarpaulin, and temporary access roads should be protected by crushed stone or gravel, as excavation proceeds. Intercepting channels should be provided (e.g. along the crest / edge of excavation) to prevent storm runoff from washing across exposed soil surfaces. Arrangements should always be in place in such a way that adequate surface protection measures can be safely carried out well before the arrival of a rainstorm.	To minimize	Contractor		Construction	MECO	
S5.8.7	Earthworks final surfaces should be well compacted and the subsequent permanent work or surface protection should be carried out immediately after the final surfaces are formed to prevent erosion caused by rainstorms. Appropriate drainage like intercepting channels should be provided where necessary.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented
S5.8.8	Measures should be taken to minimize the ingress of rainwater into trenches. If excavation of trenches in wet seasons is necessary, they should be dug and backfilled in short sections. Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented
S5.8.9	If bentonite slurries are required for any construction works, they should be reconditioned and reused wherever practicable to minimise the disposal volume of used bentonite slurries. Temporary enclosed storage locations should be provided on-site for any unused bentonite that needs to be	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94	N/A

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	transported away after the related construction activities are completed. Requirements as stipulated in ProPECC Note PN 1/94 should be closely followed when handling and disposing bentonite slurries.						
S5.8.10	Open stockpiles of construction materials (e.g. aggregates, sand and fill material) on sites should be covered with tarpaulin or similar fabric during rainstorms.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented
S5.8.11	Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers. Discharge of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented
S5.8.12	Good site practices should be adopted to remove rubbish and litter from construction sites so as to prevent the rubbish and litter from spreading from the site area. It is recommended to clean the construction sites on a regular basis.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented
S5.8.12	 The following mitigation measures related to the transportation of the sediment should be implemented to minimize the potential water quality impact: Loading of the excavated sediment to the barge shall be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding water. 	To minimise impact from transportation of sediment	Contractor	Barging point and barges	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94	To be implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
S5.8.13	 The barge transporting the sediments to the designated disposal sites shall be equipped with tight fitting seals to prevent leakage and shall not be filled to a level that would cause overflow of materials or laden water during loading or transportation. Monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the Director of Environmental Protection (DEP). There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TMDSS. The beneficial uses of the treated effluent for other onsite activities such as dust suppression, wheel washing and general cleaning etc., can minimise water consumption and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the relevant WPCO licence. 	To minimize impact from effluent discharge	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
S5.8.14	<u>Water for Bored Piling Works</u> Water used in ground boring and drilling for site investigation or rock / soil anchoring should be re-circulated as far as practicable after sedimentation. When there is a need for final disposal, the wastewater should be discharged into storm drains via silt removal facilities.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented
S5.8.15	<u>Wheel Washing Water</u> Wash-water from wheel washing facility should have been treated by silt removal facilities before discharging into storm drains. Treated wash-water could be used as dust suppression measures as far as practicable. The section of access road between the wheel washing bay and the public road should be paved to reduce vehicle tracking of soil and to prevent silty water from entering public road and drains.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented
S5.8.16	 <u>Construction Works near Channelized</u> <u>Watercourse / Ditch</u> For minimization of potential water quality impacts from the works to nearby inland channelized watercourse/ditch near SHWSTW, the practices outlined in ProPECC Note PN 1/94 "Construction Site Drainage" and ETWB TC (Works) No.5/2005 "Protection of natural streams / rivers from adverse impacts arising from construction works" should be adopted where applicable. Relevant mitigation measures are listed below: The use of less or smaller construction plants may be specified in works area close to the inland water bodies. 	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAOTM, ProPECC PN 1/94, TMDSS	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 Temporary storage of material (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from watercourse/ditch when carrying out of the construction works. Stockpiling of construction materials and dusty materials should be covered and located away from any watercourse/ditch. Construction debris and spoil should be covered up and / or disposed of as soon as possible to avoid being washed into the nearby water receivers. Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the watercourse/ditch, where practicable. Construction effluent, site run-off and sewage should be properly collected and / or treated 						
S5.8.17 - S5.8.19	Accidental Spillage of Chemicals The Contractor should register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste)(General) Regulation, should be observed and complied. • Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be	To minimise impact from accidental spillage	Contractor	All works area	Construction phase	WPCO, EIAOTM, Waste Disposal Ordinance (WDO), Waste Disposal (Chemical Waste) (General) Regulation	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges. Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows: Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport. Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents. Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area. 						
S5.8.20 - S5.8.21	 <u>Sewerage Effluent from Construction</u> <u>Workforce</u> No discharge of sewage to the storm water system and marine water will be allowed. Adequate and sufficient portable chemical toilets should be provided in the works areas to 	To minimise impact from workforces sewage effluent	Contractor	All works area	Construction phase	WPCO, EIAO- TM, TM-DSS	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 handle sewage from construction workforce. A licensed waste collector should be employed to clean and maintain the chemical toilets on a regular basis. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the surrounding environment. 						
S5.8.22 - S5.8.24	 <u>Groundwater from Contaminated Areas,</u> <u>Contaminated Site Runoff and</u> <u>Wastewater from Land Decontamination</u> Remediation of contaminated land should be properly conducted following the recommendations of Land Contamination Assessment to be conducted in future. Any excavated contaminated material and exposed contaminated surface should be properly housed and covered to avoid generation of contaminated runoff. Open stockpiling of contaminated materials should not be allowed. Any contaminated runoff or wastewater generated from the land decontamination processes should be properly collected and diverted to wastewater treatment facilities (WTF) as necessary. The WTF shall deploy suitable treatment processes (e.g. oil interceptor / activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (such as total petroleum hydrocarbon) to an undetectable range. All treated 	To minimise impact from groundwater from contaminated areas, contaminated site run- off/wastewater from land decontamination	Contractor	All works area confirmed with land contamination	Construction Phase	WPCO, EIAOTM, TM- DSS, Guidance Note for Contaminated Land Assessment	N/A

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 effluent from the wastewater treatment system shall meet the requirements as stated in TM-DSS and should be either discharged into the foul sewers or tankered away for proper disposal. No direct discharge of groundwater from contaminated areas should be adopted. Prior to any excavation works within the potentially contaminated areas, the baseline groundwater quality in these areas should be reviewed based on the past relevant site investigation data and any additional groundwater quality measurements to be performed with reference to Guidance Note for Contaminated Land Assessment and Remediation and the review results should be submitted to EPD for examination. If the review results indicated that the groundwater should be either properly treated or properly recharged into the ground in compliance with the requirements of the TM-DSS. If wastewater treatment is to be deployed for treating the contaminated groundwater, the wastewater treatment unit shall deploy suitable treatment processes (e.g. oil interceptor / activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances 	Address					

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 (such as total petroleum hydrocarbon) to an undetectable range. All treated effluent from the wastewater treatment plant shall meet the requirements as stated in the TM-DSS and should be either discharged into the foul sewers or tankered away for proper disposal. If deployment of wastewater treatment is not feasible for handling the contaminated groundwater, groundwater recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in section 2.3 of TM- DSS. The baseline groundwater quality should be determined prior to the selection of the recharge wells, and submit a working plan to EPD for agreement. Pollution levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the recharge well. Groundwater monitoring wells should be installed near the recharge points to monitor the effectiveness of the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products 	Main Concern to Address					
	should be removed as necessary by						
	installing the petrol interceptor.						

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater						
Waste M	lanagement Implication (Construction Phase	.)	1				
S7.5.3	 Recommendations for good site practices during the construction phase include: Nomination of approved personnel, such as a site manager, to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility. Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste management and chemical waste handling procedures. Provision of sufficient waste reception/ disposal points, and regular collection of waste. Adoption of appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers. Provision of regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. Adoption of a recording system for the amount of wastes generated, recycled and disposed (including the disposal sites). 	To avoid and minimize impacts arising from waste management	Contractor	All works area	Construction phase	Waste Disposal Ordinance (WDO) and Public Cleansing and Prevention of Nuisances Regulation (Cap. 132BK)	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	Preparation of Waste Management Plan (WMP), as part of the Environmental Management Plan (EMP).						
S7.5.4	 Recommendations to achieve waste reduction are as follow: Segregate and store different types of construction related waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal. Provide separate labelled bins to segregate recyclable waste such as aluminium cans from other general refuse generated by the work force, and to encourage collection by individual collectors. Recycle any unused chemicals or those with remaining functional capacity. Maximise the use of reusable steel formwork to reduce the amount of C&D materials. Adopt proper storage and site practices to minimise the potential for damage to, or contamination of construction materials. Plan the delivery and stock of construction materials carefully to minimise the amount of waste generated. Minimize over ordering and wastage through careful planning during purchasing of construction materials. 	To minimize waste generation	Contractor	All works area	Construction phase	WDO	Implemented
S7.5.6	To minimise the impact resulting from collection and transportation of C&D materials as far as practicable, C&D	To minimise the disposal of C&D waste	Contractor	All works area	Construction phase	WDO	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	waste, such as wood, plastic, steel and other metals should be reused or recycled and, as a last resort, disposed to landfill. A suitable area should be designated within the site for temporary stockpiling of C&D materials and to facilitate the sorting process.						
S7.5.6	 Within the stockpile areas, the following measures should be taken to control potential environmental impacts or nuisance: Proper handling and storage of waste such as soil by means of covers and/or water spraying system to minimise the potential environmental impact and to prevent materials from wind-blown or being washed away. Covering materials during heavy rainfall. Locating stockpiles to minimise potential visual impacts. Minimising land intake of stockpile areas as far as possible. Adopting GPS or equivalent system for tracking and monitoring of all dump trucks engaged for the Project in recording their travel routings and parking locations to prohibit illegal dumping and landfilling of C&D materials. Keeping record and analysis of data collected by GPS or equivalent system related to travel routings and parking locations of dump trucks engaged on site 	To avoid and minimize impacts arising from waste management	Contractor	All works area	Construction phase	WDO	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
S7.5.7 - S7.5.9	General refuse should be stored in enclosed bins or compaction units separate from C&D materials and chemical waste. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D materials and chemical wastes. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light materials. The recyclable component of general refuse, such as aluminium cans, paper and cleansed plastic containers shall be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste shall be set up by the Contractor. The Contractor shall also be responsible for arranging recycling companies to collect these materials. The Contractor shall carry out an education programme for workers in avoiding, reducing, reusing and recycling of materials generation. Posters and leaflets advising on the use of the bins shall also be provided in the sites as reminders.	To avoid and minimize impacts arising from waste management	Contractor	All works area	Construction phase	WDO	Implemented
S7.5.10 - S7.5.12	If chemical wastes were to be produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer, and to follow the guidelines stated in the Code of Practice on the Packaging,	To avoid and minimize impacts arising from waste management	Contractor	All works area	Construction phase	WDO	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
S7.5.13 S7.5.14 S7.5.15	Labelling and Storage of Chemical Wastes. Appropriate containers with proper labels should be used for storage of chemical wastes. Chemical wastes should be collected and delivered to designated outlet by a licensed collector. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the CWTC, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation. Any unused chemicals or those with remaining functional capacity should be collected for reuse as far as practicable. The sediment should be excavated, handled, transported and disposed of in a manner that would minimise adverse environmental impacts. For minimization of sediment disposal, beneficial reuse will be considered on site as far as practicable during the construction stage before the disposal of excavated sediment. Requirements of the Air Pollution Ordinance (Construction Dust) Regulation, where relevant, shall be adhered to during excavation, transportation and disposal of sediments. In order to minimise the exposure to	To avoid and minimize impacts arising from waste management	Contractor	All works area	Construction phase	APCO EDO	N/A
07.0.10	contaminated materials, workers shall, when necessary, wear appropriate	minimize impacts arising from		area	phase		

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	personal protective equipments (PPE) when handling contaminated sediments. Adequate washing and cleaning facilities shall also be provided on site.	waste management					
S7.5.16	For off-site disposal, the basic requirements and procedures specified under PNAP No. 252 (ADV-21) shall be followed. Marine Fill Committee (MFC) of CEDD is managing the disposal facilities in Hong Kong for the excavated sediment, while EPD is the authority of issuing marine dumping permit under the Dumping at Sea Ordinance (DASO).	To avoid and minimize impacts arising from waste management	Contractor	All works area	Construction phase	WDO, DASO, ADV-21	N/A
S7.5.17	For the purpose of site allocation and application of marine dumping permit and if considered necessary by EPD (Marine Dumping Section), separate SSTP shall be submitted to EPD for agreement under DASO. Additional SI works, based on the SSTP, shall then be carried out in order to confirm the disposal arrangements of the excavated sediment. A Sediment Quality Report (SQR), reporting the chemical and biological screening results and the estimated quantities of sediment under different disposal options, shall then be submitted to EPD for agreement under DASO.	To avoid and minimize impacts arising from waste management	Contractor	All works area	Construction phase	WDO, DASO, ADV-21	N/A
S7.5.18	To ensure disposal space is allocated for the Project, the Project Proponent should be responsible for obtaining agreement from MFC on the allocation of the disposal site. The contractor(s), on the other hand, should be responsible for the application of the marine dumping permit under DASO from EPD for the sediment disposal.	To avoid and minimize impacts arising from waste management	Project Proponent and Contractor	All works area	Construction phase	WDO, DASO, ADV-21	N/A

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
S7.5.19	The excavated sediments is expected to be loaded onto the barge at public barging point of which the exact location will be determined by the contractor(s) and agreed by EPD/CEDD and transported to the designated disposal sites allocated by MFC. The excavated sediment would be disposed of according to its determined disposal options and PNAP No. 252 (ADV-21).	To avoid and minimize impacts arising from waste management	Project Proponent and Contractor	All works area	Construction phase	WDO, DASO, ADV-21	N/A
S7.5.20	Stockpiling of contaminated sediments shall be avoided as far as possible. If temporary stockpiling of contaminated sediments is unavoidable, the excavated sediment shall be covered by tarpaulin and the area shall be placed within earth bunds or sand bags to prevent leachate from entering the ground, nearby drains and/or surrounding water bodies. The stockpiles shall be completely paved or covered by linings in order to avoid contamination to underlying soil or groundwater. Separate and clearly defined areas shall be provided for stockpiling of contaminated and uncontaminated materials. Leachate, if any, shall be collected and discharged according to the Water Pollution Control Ordinance (WPCO).	To avoid and minimize impacts arising from waste management	Contractor	All works area	Construction phase	WPCO	N/A
S7.5.21	In order to minimise the potential odour / dust emissions during excavation and transportation of the sediment, the excavated sediments shall be wetted during excavation / material handling and shall be properly covered when placed on trucks or barges. Loading of the excavated sediment to the barge shall be controlled to avoid splashing and	To avoid and minimize impacts arising from waste management	Contractor	All works area	Construction phase	WDO, APCO	N/A

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	overflowing of the sediment slurry to the surrounding water.						
S7.5.22	The barge transporting the sediments to the designated disposal sites shall be equipped with tight fitting seals to prevent leakage and shall not be filled to a level that would cause overflow of materials or laden water during loading or transportation. In addition, monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the DEP.	To avoid and minimize impacts arising from waste management	Contractor	All works area	Construction phase	WSO	N/A
Land Cor	ntamination	L	L		I.		
S8.9.3	 To minimise environmental impacts arising from the handling of potentially contaminated materials, the following environmental precautionary measures are recommended to be utilised during the course of any required site remediation: Excavation profiles must be properly designed and executed with attention to the relevant requirements for environment, health and safety. Establish and maintain a Health and Safety Plan with the information below before commencement of the SI: (a) Instruction of works on work procedures, safe practices, emergency duties, and applicable regulations; (b) Regularly scheduled meetings of the workers in which the possible hazards, problems of the job, 	To control land remediation work	Contractor	Area identified with land contamination	Prior to the commencement of construction works at the contaminated areas	"Guidance Note for Contaminated Land Assessment And Remediation", "Guidance Manual for Use of Risk- based Remediation Goals for Contaminated Land Management", "Public Cleansing and Prevention of Nuisances	N/A

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 and related safe practices are emphasized and discussed; (c) Good housekeeping practices; and (d) Availability of and instruction in the location, use and maintenance of personal protective equipment. Excavation shall be carried out during dry season as far as possible to minimise contaminated runoff from contaminated soils. Supply of suitable clean backfill material (or treated soil) after excavation. Stockpiling site(s) shall be lined with impermeable sheeting and bunded. Stockpiles shall be fully covered by impermeable sheeting to reduce dust emission. If this is not practicable due to frequent usage, regular watering shall be avoided on stockpiles of contaminated runoff. Vehicles containing any excavated materials shall be suitably covered to limit potential dust emissions or contaminated wastewater run-off, and truck bodies and tailgates shall be sealed to prevent any discharge during transport or during wet conditions. Speed control for the trucks carrying contaminated materials shall be enforced. 					Regulation (Cap. 132BK)", APCO, WDO and WPCO	

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 Vehicle wheel and body washing facilities at the site's exist points shall be established and used. Pollution control measures for air emissions (e.g. from biopile blower and handling of cement), noise emissions (e.g. from blower or earthmoving equipment), and water discharges (e.g. runoff control from treatment facility) shall be implemented and complied with relevant regulations and guidelines. 						
Landsca S9.8.1	pe and Visual Impact (Construction Phase) Trees unavoidably affected by the works should be transplanted as far as possible in accordance with DEVB TC(W) 7/2015 – Tree Preservation or LAO PN 7/2007 - Tree Preservation and Tree Removal Application for Building Development in Private Projects where applicable.	To transplant affected trees	Contractor	All works area	Construction phase	DEVB TC(W) No. 7/2015 or LAO PN 7/2007 where applicable	N/A
S9.8.1	Control of night-time lighting glare.	To minimize the Landscape and visual impact on surrounding setting	Contractor	All works area	Construction phase	TM-EIAO	N/A
S9.8.1	Erection of decorative screen hoarding which should be compatible with the surrounding setting	To minimize the Landscape and visual impact on surrounding setting	Contractor	All works area	Construction phase	TM-EIAO	N/A
S9.8.1	Management of facilities on work sites by controlling the height and disposition/arrangement of all facilities on the works site to minimize visual impact to adjacent VSRs.	To minimize visual impact to adjacent VSRs.	Contractor	All works area	Construction phase	-	Implemented
S9.8.1	All hard and soft landscape areas disturbed temporarily during construction should be reinstated on like-to-like basis,	To minimize the landscape impact	Contractor	All works area	Construction phase	-	N/A

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures and Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	to the satisfaction of the relevant	on surrounding					
	Government Departments.	setting					
Hazard to	o Life						
S10.7.2	Precautionary measures for chlorine released from SHWWTW such as provision of emergency plan for efficient evacuation including good practice (i.e. adequate training and drills for construction workers) during construction phase shall be implemented to further reduce the risk level.	To further reduce the risk level	Contractor	All works area	Construction phase	TM-EIAO	N/A

Appendix B

Monthly EM&A Report for May 2023 – Cable Bridges and Associated Civil Works for Cable Diversion Works Contract 1732





MTR Corporation Limited

Siu Ho Wan Depot Property Development -

Cable Bridges and Associated Civil Works for Cable Diversion

Monthly EM&A Report

(Period from 1 to 31 May 2023)

	Name	Signature
Prepared by	Kako Ho	Ho
Checked & Reviewed by	F. C. Tsang	Toang Jan Bearg



TABLE OF CONTENTS

EXECUTIVE SUMMARY

1.	BASIC PROJECT INFORMATION	3
2.	Environmental Status	5
3.	MONITORING RESULTS	8
4.	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS	11
5.	EM&A SITE INSPECTION	12
6.	FUTURE KEY ISSUES	13
7.	CONCLUSION AND RECOMMENDATIONS	14



LIST OF APPENDICES

- A. Construction Programme
- B. Project Organization Chart
- C. Alignment and Works Area for Contract No. 1732
- D. Location Plan of Air Quality Monitoring Station
- E. Calibration Certificate (Air Quality Monitoring)
- F. Monitoring Data (Air Quality Monitoring)
- G. Waste Flow Table
- H. Complaint Handling Procedure
- I. Event-Action Plan (Air Quality Monitoring)
- J. Statistics on Complaint, Notification of Summons and Successful Prosecution
- K. Environmental Mitigation Implementation Schedule (EMIS)
- L. Monitoring Schedule of the Reporting Month
- M. Monitoring Schedule of the Coming Month



EXECUTIVE SUMMARY

- A.1 This is the 18th monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A works carried out during the reporting period from 1 May to 31 May 2023.
- A.2 A summary of the construction works reported by the Contractor for the Project during the reporting month is listed below.

Construction activities undertaken

- General survey works
- Instrumentation monitoring
- AB11 modification works
- Cable brackets construction along trackside
- Pier and truss installation for the cable bridges (Mainly post erection closure work, openings on the piers, E&M works in the bridge)
- Draw pits, ducting and cable trough installation
- A.3 A summary of regular construction dust monitoring activities in this reporting period is listed below:

Construction dust (1-hour TSP) monitoring

DM1

15 times

- A.4 Weekly environmental site inspections were conducted during the reporting period. A joint site inspection with the IEC was carried out on 8 May 2023. No observation was reported during the site inspections. All items are rectified within the reporting period. The environmental performance of the Project was considered satisfactory.
- A.5 Details of waste management are presented in **Section 3**.
- A.6 No Action or Limit Levels exceedance of 1-hour TSP was recorded during the reporting period.
- A.7 No complaint or non-compliance was reported in the reporting period.
- A.8 No notification of summon or prosecution was received in this reporting period.
- A.9 No changes of EM&A programme were made in this reporting period.



A.10 A summary of the construction activities provided by the Main Contractor in the next three reporting months are listed below:

Construction Activities to be undertaken

- Instrumentation installation and monitoring
- General survey works
- AB11 modification works
- Erection of cable bridge and link bridges
- Cable trench and draw-pit works along the south road
- EVA construction and watermain installation near AB23
- Additional footings and plinth
- Additional civil provisions for standalone CCTV monitoring for EVA at East Level Crossing



1. BASIC PROJECT INFORMATION

- 1.1.1. The Project involves the construction of the foundations and superstructure for two cable bridges and each of two spans across and above the Tung Chung Line, Airport Express Line and the Siu Ho Wan Depot test track. The Works enable the diversion of the existing utilities to provide space for the future foundation works of the Siu Ho Wan Property Development and Oyster Bay Station (OYB, formerly named as Siu Ho Wan Station (SHO)).
- 1.1.2. The (AEIAR-214/2017) "Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works" Environmental Impact Assessment Report was approved with conditions by the Environmental Protection Department (EPD) on 29 November 2017. The latest Environmental Permit (No. EP-588/2021) was issued by the EPD on 22 March 2021.
- 1.1.3. The Project (Contract 1732) was awarded to Paul Y. CRCCI Joint Venture (JV). JV has engaged Acuity Sustainability Consulting Limited as the Environmental Team (ET) for this contract.
- 1.1.4. The Project covers the following construction activities:
 - (a) Site formation, tree removal, site safety fencing and supply and installation of Engineer's Site Accommodation;
 - (b) Diversion of existing above ground watermains to create working areas within the site for the Works;
 - (c) Constructing foundations comprising pre-bored H-piles, and carrying out pile load tests on selected H-piles;
 - (d) Constructing pile caps and spread footing foundations in shallow excavation;
 - (e) Prefabrication of steel truss vertical support frames, and erection on the foundations;
 - (f) Prefabrication of steel truss cable bridges and erection on to the vertical support frames;
 - (g) Prefabrication and erection of a steel link bridge spanning between the cable bridge and the façade of the existing building AB11;
 - (h) Installation of cable trays, cable supports and sunshield in and along the cable bridges, vertical support frames and at external walls of the existing building AB11;
 - (i) Installation of cable bridge miscellaneous details such as roof, drainage, facades, lightings, lightning protection, access control;
 - (j) Installation of ground level cable troughs;
 - (k) Modification of the façade of existing AB11 building for cable feeding out from the building;
 - (1) All temporary railway protection works such as hoardings and retaining structures in course of the Execution of the works; and
 - (m) Supply and installation of equipotential bonding for the cable bridge and associated fixed metal parts attached to the cable bridge.



1.1.5. A summary of the major construction activities undertaken in this reporting period (from 1 May to 31 May 2023) is shown in Table 1.1. The construction programme is presented in Appendix A.

Table 1.1Summary of the construction activities reported by Main Contractor during
the Reporting Month

Construction Activities undertaken

- General survey works
- Instrumentation monitoring
- AB11 modification works
- Cable brackets construction along trackside
- Pier and truss installation for the cable bridges (Mainly post erection closure work, openings on the piers, E&M works in the bridge)
- Draw pits, ducting and cable trough installation
- 1.1.6. The project organisational chart specifying management structure and contact details are shown in **Appendix B**.
- 1.1.7. A summary of the valid permits, licences, and/ or notifications on environmental protection for this Project is presented in **Table 1.2**.

Table 1.2Summary of the Status of Valid Environmental License Notification, Permit
and Documentations

Permit/ Licences/	Valid Period		S 44					
Notification/ Reference No.	From	То	Status	Remark				
Environmental Permit								
EP-588/2021	22 Mar 2021	N/A	Valid	-				
Wastewater Discharge Lie	Wastewater Discharge License							
WT00040639-2022	23 Mar 2022	31 Mar 2027	Valid	-				
Notification of Constructi Regulation	Notification of Construction Works under the Air Pollution Control (Construction Dust) Regulation							
Ref. 472845	N/A	N/A	Notified	Notification submitted on 19 Oct 2021				
Chemical Waste Producer	Registration							
WPN5213-961-P3457-01	19 Nov 2021	N/A	Valid	-				
Billing Account for Dispos	sal of Construct	tion Waste						
7042328	25 Nov 2021	N/A	Valid	-				
Construction Noise Permi	t			·				
GW-RS0240-23	23 Mar 2023	19 Sep 2023	Valid	Site office and main works at AB11 area and cross-track area, cable bracket works, and additional EI works				



2. Environmental Status

2.1.1. Environmental permit (EP) conditions under the EIAO, submission status under the EP and implementation status of mitigation measures had been reviewed and implemented on schedule. The status of required submissions under the EP (No. EP-588/2021) as of the reporting period for the Project are summarised in **Table 2.1**.

EP Condition (EP-588/2021)	Submission	Submission date	
	Commencement Date of	11 June 2021 (1 st submission)	
1.12	Construction	12 July 2021 (2 nd submission)	
		12 August 2021 (3 rd submission)	
		1 November 2021 (1 st submission)	
2.7	Construction Works Phasing Schedule	20 December 2021 (2 nd submission)	
	Schedule	29 December 2021 (Deposited)	
2.9	Environmental Permit Submission	12 August 2021	
2.8	Schedule	10 September 2021 (Deposited)	
		1 November 2021 (1 st submission)	
		20 December 2021 (2 nd submission)	
2.9	Management Organization	21 April 2022 (3 rd submission)	
		9 August 2022 (4 th submission)	
		16 November 2022 (5 th submission)	
		1 November 2021 (1 st submission)	
		20 December 2021 (2 nd submission)	
		28 December 2021 (Deposited)	
2.10	Construction Noise Mitigation	30 December 2022 (1 st submission*)	
	Plan	29 March 2023 (2 nd submission for	
		Phase 1 work)	
		18 May 2023 (3 rd submission for Phase 1 work)	
2.11	Noise Mitigation Plan	31 March 2023 (1 st submission)	
		1 November 2021 (1 st submission)	
2.13	Waste Management Plan	20 December 2021 (2 nd submission)	
		28 December 2021 (Deposited)	
2.15	Landscape and Visual Plan(s)	27 April 2023 (1 st submission)	
2.2	Deschart D	1 November 2021	
3.3	Baseline Monitoring Report	16 November 2021 (Deposited)	
3.4	Monthly EM&A Report (December 2021)	13 January 2022	

 Table 2.1
 Summary of Status of Required Submission for EP-588/2021 for the Project



EP Condition (EP-588/2021)	Submission	Submission date
3.4	Monthly EM&A Report (January 2022)	15 February 2022
3.4	Monthly EM&A Report (February 2022)	10 March 2022
3.4	Monthly EM&A Report (March 2022)	19 April 2022
3.4	Monthly EM&A Report (April 2022)	16 May 2022
3.4	Monthly EM&A Report (May 2022)	14 June 2022
3.4	Monthly EM&A Report (June 2022)	14 July 2022
3.4	Monthly EM&A Report (July 2022)	12 August 2022
3.4	Monthly EM&A Report (August 2022)	14 September 2022
3.4	Monthly EM&A Report (September 2022)	14 October 2022
3.4	Monthly EM&A Report (October 2022)	14 November 2022
3.4	Monthly EM&A Report (November 2022)	14 December 2022
3.4	Monthly EM&A Report (December 2022)	13 January 2023
3.4	Monthly EM&A Report (January 2023)	14 February 2023
3.4	Monthly EM&A Report (February 2023)	14 March 2023
3.4	Monthly EM&A Report (March 2023)	18 April 2023
3.4	Monthly EM&A Report (April 2023)	15 May 2023
3.4	Monthly EM&A Report (May 2023)	To be submitted within 10 working days after the end of the reporting month
4.2	Dedicated Internet Website	12 January 2022

* A new version of Construction Noise Mitigation Plan was submitted to the EPD on 30 December 2022 to cover the Phase 1 works.



2.1.2. The drawings showing the project layout and the location of the monitoring station are attached in **Appendix C** and **Appendix D**, respectively. A summary of the monitoring location is shown in **Table 2.2**.

Table 2.2 Summary of the location of the monitoring station

Air Sensitive Receiver (ASR) ID No. in EIA Report	Monitoring Station ID	ASR Description
A2	DM1	Siu Ho Wan Government Maintenance Depot



3. MONITORING RESULTS

3.1. Monitoring Parameters

Air Quality

- 3.1.1. The impact monitoring had been carried out in accordance with Section 2.6 of the approved EM&A Manual, with sampling frequency of at least 3 times in every 6 days undertaken, to determine the 1-hour total suspended particulates (TSP) levels at the monitoring locations in the reporting period.
- 3.1.2. General meteorological conditions (wind speed, direction and precipitation) and notes regarding any significant adjacent dust producing sources had also been recorded throughout the impact monitoring period.

3.2. Monitoring Equipment and Methodology

Monitoring Equipment

- 3.2.1. Portable direct reading dust meter was used to carry out the 1-hour TSP monitoring. Portable direct reading dust meters used in this monitoring were proven to the IEC to be capable of achieving comparable result as that of the HVS and, thus, were used for sampling.
- 3.2.2. The equipment used for 1-hour TSP measurement during the reporting month are summarised in **Table 3.1**.

Measuring	Monitoring	Brand and Model	Serial	Date of
Parameter	Equipment		Number	Calibration
1-hour TSP	Portable direct reading dust meter (1-hour TSP)	Sibata Digital Dust Monitor (Model No. LD-3B)	A.005.16a	26 Apr 2023

 Table 3.1
 Construction Dust Monitoring Equipment

3.2.3. The portable direct reading dust meter was calibrated at 1-year interval against a High-Volume Sampler, TE-5170. Copies of calibration certificates of the portable direct reading dust meter are presented in **Appendix E.**

Monitoring Methodology

- 3.2.4. The 1-hour TSP measurement followed manufacturer's instruction manual. Before initiating a measurement, zeroing the portable direct reading dust meter was carried out to ensure maximum accuracy of concentration measurements.
- 3.2.5. The 1-hour TSP was sampled by drawing air into the portable direct reading dust meter where particular concentrations were measured instantaneously with an in-built silicon detector sensing light scattered by the particulates in the sampled air. Continuous TSP levels were indicated and logged by a built-in data logger compatible with Windows based program to facilitate data collection, analysis and reporting.



3.3. Monitoring Location

3.3.1. Location of the designated dust monitoring station is described in Table 3.2.

Monitoring Station ID	Dust Monitoring Station
DM1	Siu Ho Wan Government Maintenance Depot

3.4. Result Summary

- 3.4.1. Dust impact monitoring was carried out at DM1 on 4, 10, 16, 22 and 27 May 2023 during the reporting month (**Appendix L**). According to the field observations, the major dust sources identified included vehicular emissions from North Lantau Highway and Cheung Tung Road. Gentle wind was recorded throughout the monitoring period, with gentle to strong wind recorded occasionally.
- 3.4.2. The results for 1-hour TSP are summarized in **Table 3.3**. The measurement data are presented in **Appendix F.**

Monitoring	Range	Action Level	Limit Level	No. of Exceedances
Location	(µg/m ³)	(µg/m ³)	(µg/m ³)	
DM1	58.9 - 63.3	294.7	500	0

 Table 3.3
 Summary of 1-hour TSP Monitoring Results

Waste management

3.4.3. The waste generated from this Project includes inert C&D materials, and non-inert C&D materials. Non-inert C&D materials are made up of general refuse, vegetative wastes and recyclable wastes such as plastics and paper/ cardboard packaging waste. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in **Table 3.4**. Details of cumulative waste management data are presented as a waste flow table in **Appendix G**.



Table 3.4 Quantities of waste generated from the Project

				Quantity			
				Non-in	ert C&D mate	erials	
Reporting period	Inert C&D materials (in m ³)	Chemical Waste (in '000 kg)	Others, e.g., General Refuse		Recycled	wastes	
	(111 1117)		disposed at Landfill (in '000 kg)	Paper/ cardboard (in '000 kg)	Plastics (in '000 kg)	Metals (in '000 kg)	Yard Waste (in '000 kg)
May 2023	483.460	0.000	9.350	0.000	0.000	0.000	0.000

- 3.4.4. All dump trucks for C&D materials transportation and disposal were equipped with Global Positioning System (GPS) for real time tracking and monitoring their travel routings and parking locations in order to avoid illegal dumping or landfilling of C&D materials.
- 3.4.5. The GPS data including travel routings of dump trucks was reviewed by the ET and IEC, and no illegal dumping activities were suspected.



4. SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS

- 4.1.1. The Environmental Complaint Handling Procedure is shown in Appendix H.
- 4.1.2. Should non-compliance of the air quality criteria occur, action in accordance with the Event and Action Plan in **Appendix I** shall be carried out.
- 4.1.3. No Action and Limit Levels exceedance of 1-hour TSP was recorded during the reporting month.
- 4.1.4. No complaint or non-compliance was reported in the reporting month.
- 4.1.5. No notification of summons and prosecution was received in the reporting period.
- 4.1.6. Statistics on complaints, notifications of summons and successful prosecutions are summarized in **Appendix J**.



5. EM&A SITE INSPECTION

5.1.1. Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, five (5) site inspections were carried out on 2, 8, 15, 22 and 29 May 2023. One joint site inspection with the IEC was also undertaken on 8 May 2023. No observation was reported during the weekly site inspections. Key observations during the site inspections are summarized in **Table 5.1**.

Date	Observation/ Recommendation	Follow-up Status
2 May 2023	None	None
8 May 2023	None	None
15 May 2023	None	None
22 May 2023	None	None
29 May 2023	None	None

Table 5.1Site Observations

5.1.2. According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents are implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix K**.



6. **FUTURE KEY ISSUES**

6.1.1. Work to be undertaken in the next three reporting months are:

Construction Activities to be undertaken

- Instrumentation installation and monitoring
- General survey works
- AB11 modification works
- Erection of cable bridge and link bridges
- Cable trench and draw-pit works along the south road
- EVA construction and watermain installation near AB23
- Additional footings and plinth
- Additional civil provisions for standalone CCTV monitoring for EVA at East Level Crossing
- 6.1.2. Potential environmental impacts arising from the above construction activities are mainly associated with construction dust impact, noise impact, and waste management.
- 6.1.3. The tentative schedule of regular 1-hour TSP monitoring in the next reporting period is presented in **Appendix M**.
- 6.1.4. The construction programme for the Project for the next reporting month is presented in **Appendix A**.



7. CONCLUSION AND RECOMMENDATIONS

- 7.1.1. This 18th monthly EM&A Report presents the EM&A works undertaken during the period from 1 May to 31 May 2023 in accordance with the EM&A Manual and the requirement under EP-588/2021.
- 7.1.2. Air quality (including 1-hour TSP) impact monitoring was carried out in the reporting period. No exceedance of the Action and Limit Levels was recorded for air quality impact monitoring during the reporting period.
- 7.1.3. Weekly environmental site inspections were conducted during the reporting period. A joint site inspection with the IEC was carried out on 8 May 2023. No observation was reported during the site inspections. All items are rectified within the reporting period. The environmental performance of the Project was considered satisfactory.
- 7.1.4. No complaint or non-compliance was reported in the reporting month.
- 7.1.5. No notification of summons or prosecution was received in the reporting month.
- 7.1.6. The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.
- 7.1.7. No change of EM&A programme was made in this reporting period.
- 7.1.8. The proposed mitigation measures were properly implemented and were considered effective and efficient in pollution control.



Appendix A Construction Programme



Appendix A Construction Programme


Construction Activities		2021						2022						2023														
Construction Activities	ID	J	F 1	M A	M	J.	ΙA	S	0	N D	J	F 1	M A	M	J	JA	A S	0	N	D	JF	M	A N	4 J	J	A S	0	N D
Contract 1732 - Cable Bridge and Associated Civil Works for Cable Diversion	2																											
Site Clearance & Hoarding / UU / Cable Trenches	2.1																											
H-piling	2.2																											
Excavation (Soil)	2.3																											
Substructure (footing, pile caps, columns)	2.4																											
Backfilling	2.5																											
Superstructure (Cable Bridges)	2.6																											






Appendix B Project Organization Chart



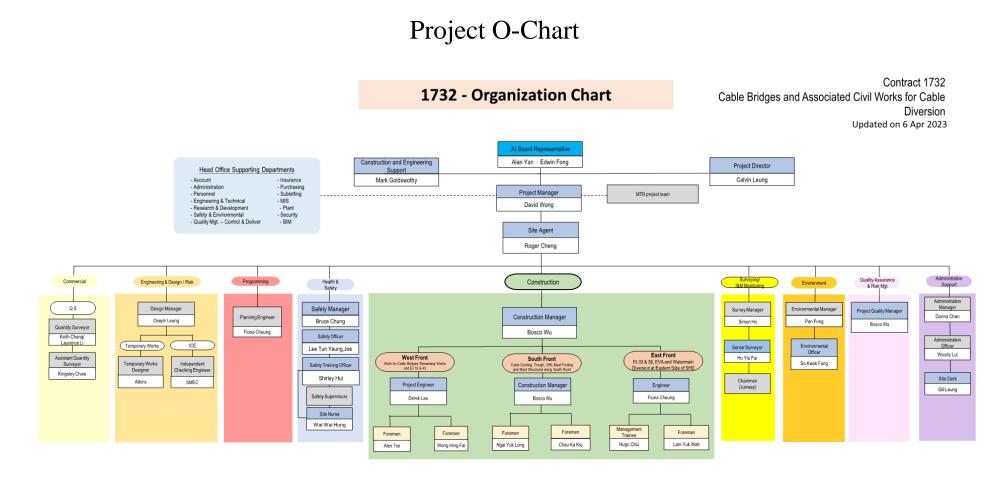





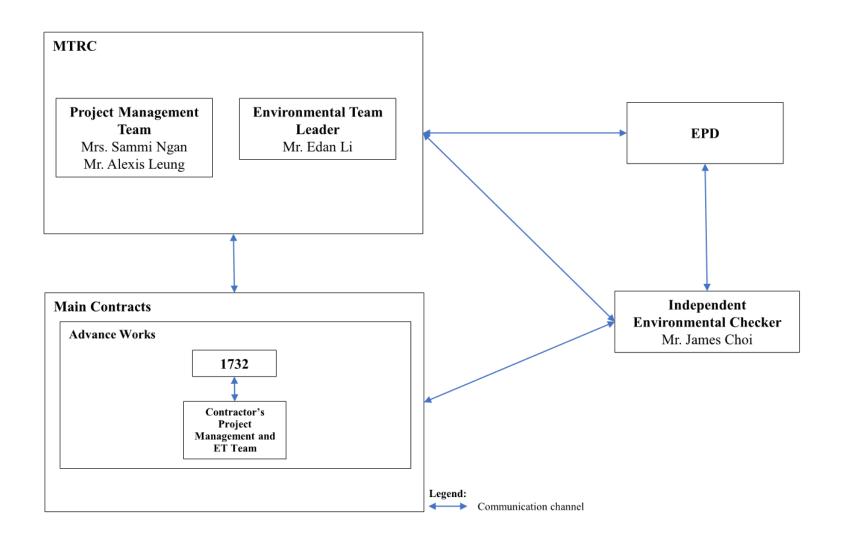



MTR's Contact:

MTRC - Project Management Team										
Position	Name	Telephone								
Chief Construction Manager - OYB	Mrs. Sammi Ngan	2208 3753								
Senior Construction Manager - Civil	Mr. Alexis Leung	2208 3968								

MTRC - Environmental Team									
Position	Name	Telephone							
Environmental Team Leader	Mr. Edan Li	2688 1179							
Environmental Team Member	Mr. Cyrus Lau	2688 1585							

ANewR Consulting Limited - IEC		
Position	Name	Telephone
Independent Environmental Checker	Mr. James Choi	2618 2836

Contractor's Contact:

Main Works Contract	Description	Contractor	Position	Name	Telephone
	Construction of cable bridges and		Project Manager	David Wong	9712 9984
1732	associated civil works for cable		Environmental Officer	Pan Fong	9436 9435
	diversion	Joint Venture	Environmental Team Leader	Tsang, Fan Cheong	2698 8060






Appendix C

Alignment and Works Area for Contract No. 1732




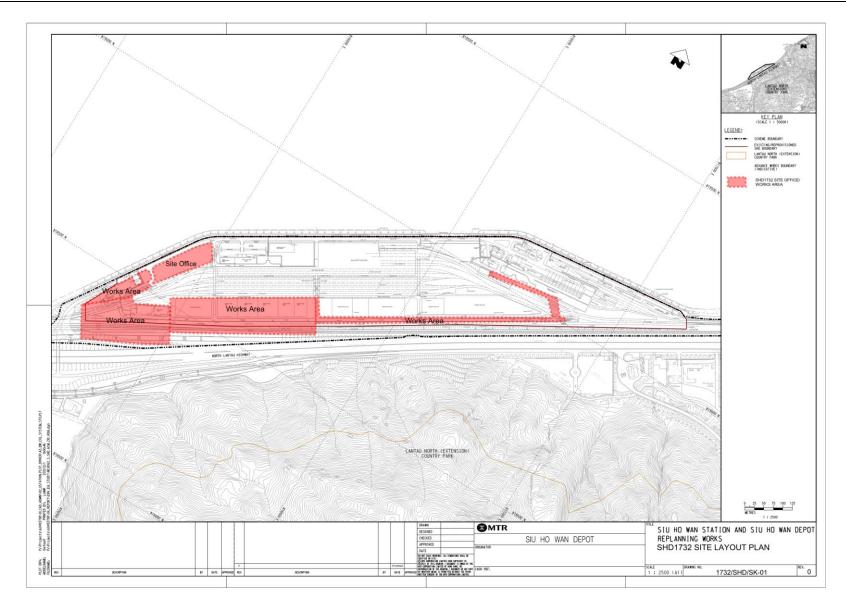



Appendix D Location Plan of Air Quality Monitoring Station



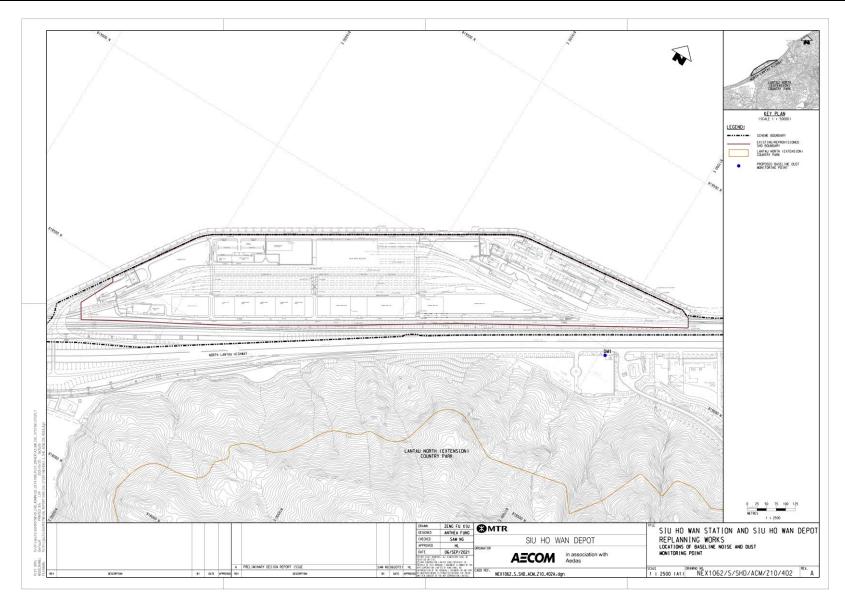





Appendix E Calibration Certificates (Air Quality Monitoring Equipment)



EQUIPMENT CALIBRATION RECORD

Type:			Laser Dus	t Monitor			
	urer/Brand:		SIBATA				
Model No			LD-3B				
Equipmer			A.005.16a	4			
	Adjustment Sca	le Setting:	521 CPM				
Scholenne	, ajustinent seu	le setting.	521 01 11				
Operator:			WS CHAN				
Standard	Equimment						
	•						I
Equipmer	it:		High Volu	me Samp	er		
Venue:			Pedestria	n Plaza			•
Model No	.:		TE-5170				•
Serial No.	:		10273				
Last Calib	ration Date:		4-Apr-23				
Calibratio	n Result						
	v Adjustment Sca	•				521	CPM
Sensitivity	v Adjustment Sca	le Setting (After	Calibratio	n):		521	CPM
	1						
Hour	Date	Time		Condition	Concentration (1)	Total Count(2)	Count/
	(dd/mm/yy)		Temp (°C)	R.H.(%)	(mg/m3)		Minute(3)
1	26/04/22	0.00.10.00	22.5	65	Y-axis	1000	X-axis
1	26/04/23	9:00-10:00	23.5	65	0.0490	1860	31.00
2	26/04/23	10:00-11:00	23.5	65	0.0500	1940	32.33
3	26/04/23	11:00-12:00	23.5	65	0.0520	2020	33.67
4	26/04/23	12:00-13:00	23.5	65	0.0540	2150	35.83
Note:	¥ -	data was measu	, -		Sampler		
	ž	was logged by L			N		
	(3) Count/minu	ite was calculate	ed by (Tota	Count/60))		
Bylinear	Regression of Y o	n V					
by Lillear	Slope (K-factor)		0.0015				
	Correlation coe		0.9997				
	correlation coe	mcient.	0.9997				
Validity of	f Calibration Reco	ord:	26-A	pr-24			
Remarks:							
Neniarks:							

QC Reviewer:

Y.W. Fung

1/ Signature:






Appendix F Monitoring Data (Air Quality Monitoring)





The Summary of 1-hour TSP Concentration ($\mu g/m^3$) at Location DM1

Data	Weether	Start Time	1 st Hour	2 nd Hour	3 rd Hour
Date	Weather	(hh:mm)	μg/m ³	μg/m ³	μg/m ³
4 May 23	Sunny	11:05	60.2	62.8	63.3
10 May 23	Sunny	11:00	60.6	61.8	60.2
16 May 23	Fine	13:45	58.9	61.1	62.0
22 May 23	Fine	10:50	59.5	60.9	61.1
27 May 23	Fine	11:10	62.2	61.3	62.4
Mir	nimum: 58.9 μ	g/m ³	Ma	ximum: 63.3 µg	g/m ³

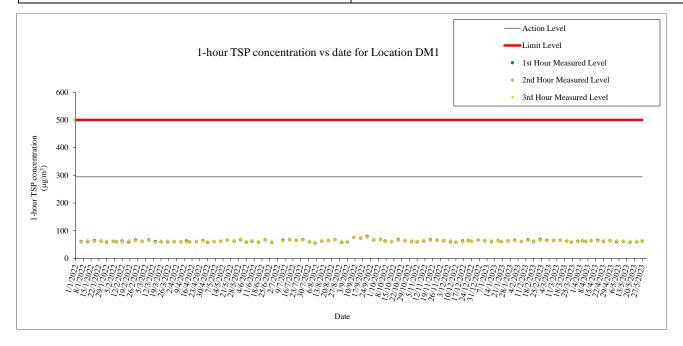





Appendix G Waste Flow Table



Monthly Summary Waste Flow TableName of Department:MTRContract No. / We stered for Man 2022

Contract No. / Works Order No.: <u>1732</u>

Monthly Summary Waste Flow Table for May 2023

	Actual Quantities of Inert Construction Materials Generated Monthly							
Month	(a) Total Quantity Generated	(b) Hard Rock and Large Broken Concrete	(c) Reused in the Contract	(d) Reused in other Projects	(e) Disposed of as Public Fill	(f) Imported Fill		
	(in m ³)	(in m ³)	(in m ³)	(in m ³)	(in m ³)	(in m ³)		
Jan-23	0.000	0.000	0.000	0.000	0.000	0.000		
Feb-23	325.581	130.876	0.000	0.000	194.705	0.000		
Mar-23	762.706	168.656	0.000	0.000	594.050	0.000		
Apr-23	229.563	87.508	0.000	0.000	142.055	0.000		
May-23	483.460	0.000	0.000	0.000	483.460	0.000		
Jun-23								
Sub-total	1801.310	387.040	0.000	0.000	1414.270	0.000		
Jul-23								
Aug-23								
Sep-23								
Oct-23								
Nov-23								
Dec-23								
Total	1801.310	387.040	0.000	0.000	1414.270	0.000		
2021	0.000	0.000	0.000	0.000	0.000	0.000		
2022	1226.473	72.128	0.000	0.000	1154.345	0.000		
Accumulated Total	3027.783	459.168	0.000	0.000	2568.615	0.000		




	Actual Quantities of <u>Non-inert</u> Construction Materials Generated Monthly							
Month	(g) Metals	(h) Paper/ cardboard packaging	(i) Plastics	(j) Chemical Waste	(k) Recyclable Yard Waste	(1) Others, e.g. General Refuse disposed of at Landfill		
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)		
	generated	generated	generated	generated	generated	generated		
Jan-23	0.000	0.000	0.000	0.000	0.000	10.130		
Feb-23	0.000	12.500	0.000	0.000	0.000	9.190		
Mar-23	0.000	0.000	0.000	0.000	0.000	17.880		
Apr-23	0.000	0.000	0.000	0.000	0.000	12.670		
May-23	0.000	0.000	0.000	0.000	0.000	9.350		
Jun-23								
Sub-total	0.000	12.500	0.000	0.000	0.000	59.220		
Jul-23								
Aug-23								
Sep-23								
Oct-23								
Nov-23								
Dec-23								
Total	0.000	12.500	0.000	0.000	0.000	59.220		
2021	0.000	0.000	0.000	0.000	0.000	0.000		
2022	0.200	0.277	0.300	0.010	93.660	393.380		
Accumulated Total	0.200	12.777	0.300	0.010	93.660	452.600		





Appendix H Complaint Handling Procedure



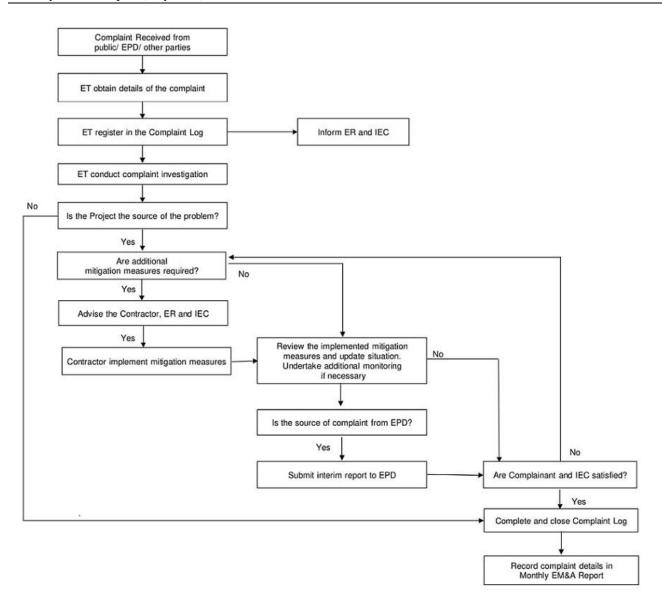





Appendix I Event-Action Plan (Air Quality Monitoring)



EVENT	ACTION							
EVENT	ET	IEC	ER	CONTRACTOR				
ACTION LEVEL			•					
Exceedance for one sample	 Repeat measurement to confirm findings; If exceedance is confirmed, inform the Contractor, IEC and ER; Identify source(s), investigate the causes of exceedance and propose remedial measures; and Increase monitoring frequency. 	 Check monitoring data submitted by the ET; Check Contractor's working method; and Discuss with ET, ER and Contractor on possible remedial measures Review and advise the ET and ER on the effectiveness of the proposed remedial measures. 	 Confirm receipt of notification of exceedance in writing. 	 Identify source(s), investigate the causes of exceedance and propose remedial measures; Implement remedial measures; and Amend working methods agreed with the ER as appropriate. 				
Exceedance for two or more consecutive samples	 Repeat measurements to confirm findings; If exceedance is confirmed, inform Contractor, IEC and ER; Identify source(s), investigate the causes of exceedance and propose remedial measures; Increase monitoring frequency to daily; Advise the Contractor and ER on the effectiveness of the proposed remedial measures; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with Contractor, IEC and ER to discuss the remedial measures to be taken; and If exceedance stops, cease additional monitoring. 	 Check monitoring data submitted by the ET; Check Contractor's working method; and Discuss with ET, ER and Contractor on possible remedial measures; Review and advise the ET and ER on the effectiveness of the proposed remedial measures; and Supervise Implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; In consultation with the ET and IEC agree with the Contractor on the remedial measures to be implemented; and Supervise implementation of remedial measures 	 Identify source(s) and investigate the causes of exceedance; Submit proposals for remedial measures to the ER, ET and IEC within three working days of notification for agreement; Implement the agreed proposals; and Amend proposal as appropriate. 				



EVENT	ACTION								
EVENI	ET	IEC	ER	CONTRACTOR					
LIMIT LEVEL									
Exceedance for one sample	 Repeat measurement to confirm findings; If exceedance is confirmed, inform the Contractor, IEC, EPD and ER; Identify source(s), investigate the causes of exceedance and propose remedial; Increase monitoring frequency to daily; and Discuss with the ER, IEC and Contractor on the remedial measures and assess effectiveness. 	 Check monitoring data submitted by the ET; Check Contractor's working method; Discuss with the ET, ER and Contractor on possible remedial measures; Review and advise the ET and ER on the effectiveness of the proposed remedial measures; and Supervise implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Review and agree on the remedial measures proposed by the Contractor; and Ensure remedial measures properly implemented. 	 Identify source(s) and investigate the causes of exceedance; Take immediate action to avoid further exceedance; Submit proposals for remedial measures to ER, ET and IEC within three working days of notification for agreement; Implement the agreed proposals; and Amend proposal if 					
Exceedance for two or more consecutive samples	 Repeat measurement to confirm findings; If exceedance is confirmed, inform IEC, ER, Contractor and EPD; Identify source(s), investigate the causes of exceedance and propose remedial measures; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and 	 Check monitoring data submitted by the ET; Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and Supervise the implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures; and If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 appropriate. Identify source(s) and investigate the causes of exceedance; Take immediate action to avoid further exceedance; Submit proposals for remedial measures to the ER, IEC and ET within three working days of notification for agreement; Implement the agreed proposals; Revise and resubmit proposals if problem still not under control; and Stop the relevant 					



	EVENT	ACTION					
		ET	IEC	ER	CONTRACTOR		
		keep IEC, EPD and ER informed of the results; and 8. If exceedance stops, cease additional monitoring.			portion of works as determined by the ER until the exceedance is abated.		

Note: ET – Environmental Team; ER – Engineer's Representative; IEC – Independent Environmental Checker



Appendix J Statistics on Complaint, Notification of Summons and Successful Prosecution



Table J1 Statistical Summary of Exceedance

Air Quality					
Location	Action Level	Limit Level	Total		
DM1 0		0	0		

Table J2 Statistical Summary of Environmental Complaint

Departing Davied	Environmental Complaint Statistics				
Reporting Period	Frequency	Cumulative	Complaint Nature		
1 May 2023 	0	0	N/A		

Table J3 Statistical Summary of Environmental Non-compliance

Departing Daried	Environmental Non-compliance Statistics				
Reporting Period	Frequency	Cumulative	Details		
1 May 2023 31 May 2023	0	0	N/A		

Table J4 Statistical Summary of Environmental Summons

Departing Davied	Environmental Summons Statistics				
Reporting Period	Frequency	Cumulative	Details		
1 May 2023 31 May 2023	0	0	N/A		

Table J5 Statistical Summary of Environmental Prosecution

Departing Devied	Environmental Prosecution Statistics				
Reporting Period	Frequency	Cumulative	Details		
1 May 2023 31 May 2023	0	0	N/A		



Appendix K Environmental Mitigation Implementation Schedule (EMIS)



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
Air Quality	y (Construction Phase)						
\$3.8.1	Watering once per hour on active works areas, exposed areas and unpaved haul roads during working hours.	To minimize dust impacts	Contractor	All works area	Construction phase	Air Pollution Control Ordinance (APCO)	Implemented
S3.8.9	 Implementation of dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices should be carried out to further minimize construction dust impact. Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. Use of frequent watering for particularly dusty construction areas and areas close to ASRs. Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines. Open stockpiles should be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations. Establishment and use of vehicle wheel and body washing facilities at the exit points of the site. 	To minimize dust impacts	Contractor	All works area	Construction phase	Air Pollution Control Ordinance (APCO)	Implemented



EIA Ref.		Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	• Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods.						
	• Imposition of speed controls for vehicles on unpaved site roads. 8 kilometres per hour is the recommended limit.						
	• Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs.						
	• Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.						
	• Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high-level alarm which is interlocked with the material filling line and no overfilling is allowed.						
	• Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system.						



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
Noise Impa	act (Construction Phase)						
S4.5.16	 Implement the following good site practices as far as practicable: Only well-maintained plant should be operated on-site, and plant should be serviced regularly during the construction program; Silencers or mufflers on construction equipment should be utilised and should be properly maintained during the construction program; Mobile plant, is any, should be sited as far from NSRs as possible; Machine and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 	To minimise impacts to surrounding habitats	Contractor	All works area	Construction phase	TM-EIAO	Implemented
\$4.5.17	Adopting quiet PME is recommended. The type of quiet PME adopted in this assessment is for reference only. The contractors may adopt alternative quiet PME as long as it can be demonstrated that they would not result in construction noise impacts worse than those predicted in this assessment.	To reduce impact to affected NSRs	Contractor	All works area	Construction phase	TM-EIAO	Implemented
S4.5.19	Use of noise barriers and noise enclosures to provide screening for construction plant where recommended.	To reduce impact to affected NSRs	Contractor	All works area	Construction phase	TM-EIAO	N/A



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
Water Qual	lity Impact (Construction Phase)						
S5.8.4	Surface and road run-off from construction sites should be discharged into storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sedimentation basins. Channels or earth bunds or sandbag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Perimeter channels should be provided on site boundaries where necessary to intercept storm run-off from outside the site so that it will not wash across the site. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	Water Pollution Control Ordinance (WPCO), Technical Memorandum on EIA Ordinance (EIAO-TM), ProPECC PN 1/94, Technical Memorandum on	Implemented
\$5.8.5	Silt removal facilities, channels and manholes should be maintained, and the deposited silt and grit should be removed regularly, at the onset of and after each rainstorm to prevent local flooding. Any practical options for the diversion and re- alignment of drainage should comply with both engineering and environmental requirements in order to provide adequate hydraulic capacity of all drains.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase		Implemented
S5.8.6	Construction works should be programmed to minimize soil excavation works in rainy seasons (April to September). If soil excavation cannot be avoided in these months or at any time of year when rainstorms are likely, for the purpose of preventing soil erosion, temporary exposed slope surfaces should be covered e.g., by tarpaulin, and temporary access roads should be protected by crushed stone or gravel, as excavation proceeds. Intercepting channels should be provided (e.g., along the crest / edge of excavation) to prevent storm runoff from washing across exposed soil surfaces. Arrangements should always be in place in such a way that adequate surface protection measures can be safely carried out well before the arrival of a rainstorm.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	Waters (TM-DSS)	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
S5.8.7	Earthworks final surfaces should be well compacted, and the subsequent permanent work or surface protection should be carried out immediately after the final surfaces are formed to prevent erosion caused by rainstorms. Appropriate drainage like intercepting channels should be provided where necessary.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase		Implemented
S5.8.8	Measures should be taken to minimize the ingress of rainwater into trenches. If excavation of trenches in wet seasons is necessary, they should be dug and backfilled in short sections. Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase		Implemented
S5.8.9	If bentonite slurries are required for any construction works, they should be reconditioned and reused wherever practicable to minimise the disposal volume of used bentonite slurries. Temporary enclosed storage locations should be provided on-site for any unused bentonite that needs to be transported away after the related construction activities are completed. Requirements as stipulated in ProPECC Note PN 1/94 should be closely followed when handling and disposing bentonite slurries.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94	N/A
S5.8.10	Open stockpiles of construction materials (e.g. aggregates, sand and fill material) on sites should be covered with tarpaulin or similar fabric during rainstorms.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	Implemented
S5.8.11	Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers. Discharge of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
S5.8.12	Good site practices should be adopted to remove rubbish and litter from construction sites so as to prevent the rubbish and litter from spreading from the site area. It is recommended to clean the construction sites on a regular basis.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	Implemented
S5.8.12	 The following mitigation measures related to the transportation of the sediment should be implemented to minimize the potential water quality impact: Loading of the excavated sediment to the barge shall be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding water. The barge transporting the sediments to the designated disposal sites shall be equipped with tight fitting seals to prevent leakage and shall not be filled to a level that would cause overflow of materials or laden water during loading or transportation. Monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the Director of Environmental Protection (DEP). 	To minimise impact from transportation of sediment	Contractor	Barging point and barges	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94	N/A
\$5.8.13	There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM- DSS. The beneficial uses of the treated effluent for other on- site activities such as dust suppression, wheel washing and general cleaning etc., can minimise water consumption and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required	To minimize impact from effluent discharge	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	Approved



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	during the construction phase of the Project, the monitoring should be carried out in accordance with the relevant WPCO licence.						
	Water for Bored Piling Works Water used in ground boring and drilling for site investigation or rock / soil anchoring should be re-circulated as far as practicable after sedimentation. When there is a need for final disposal, the wastewater should be discharged into storm drains via silt removal facilities.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	Implemented
	Wheel Washing Water Wash-water from wheel washing facility should have been treated by silt removal facilities before discharging into storm drains. Treated wash-water could be used as dust suppression measures as far as practicable. The section of access road between the wheel washing bay and the public road should be paved to reduce vehicle tracking of soil and to prevent silty water from entering public road and drains.	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	Implemented
	 Construction Works near Channelized Watercourse / Ditch For minimization of potential water quality impacts from the works to nearby inland channelized watercourse/ditch near SHWSTW, the practices outlined in ProPECC Note PN 1/94 "Construction Site Drainage" and ETWB TC (Works) No.5/2005 "Protection of natural streams / rivers from adverse impacts arising from construction works" should be adopted where applicable. Relevant mitigation measures are listed below: The use of less or smaller construction plants may be specified in works area close to the inland water bodies. Temporary storage of material (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from watercourse/ditch when carrying out of the construction works. Stockpiling of construction 	To minimise impact from construction site run-off	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS, ETWB TC(Works) No. 5/2005	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 materials and dusty materials should be covered and located away from any watercourse/ditch. Construction debris and spoil should be covered up and / or disposed of as soon as possible to avoid being washed into the nearby water receivers. Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the watercourse/ditch, where practicable. Construction effluent, site run-off and sewage should be properly collected and / or treated. 						
S5.8.17 – S5.8.19	 Accidental Spillage of Chemicals The Contractor should register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation, should be observed and complied. Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges. Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. General requirements to deal with chemical wastes. General requirements are given as follows: Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during 	To minimise impact from accidental spillage	Contractor	All works area	Construction phase	WPCO, EIAO- TM, Waste Disposal Ordinance (WDO), Waste Disposal (Chemical Waste) (General) Regulation	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 storage, handling and transport. Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents. Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area. 						
<u>\$5.8.22</u> <u>\$5.8.24</u>	 Groundwater from Contaminated Areas, Contaminated Site Runoff and Wastewater from Land Decontamination Remediation of contaminated land should be properly conducted following the recommendations of Land Contamination Assessment to be conducted in future. Any excavated contaminated material and exposed contaminated surface should be properly housed and covered to avoid generation of contaminated runoff. Open stockpiling of contaminated materials should not be allowed. Any contaminated runoff or wastewater generated from the land decontamination processes should be properly collected and diverted to wastewater treatment facilities (WTF) as necessary. The WTF shall deploy suitable treatment processes (e.g., oil interceptor/ activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (such as total petroleum hydrocarbon) to an undetectable range. All treated effluent from the wastewater treatment system shall meet the requirements as stated in TM-DSS and should be either discharged into the foul sewers or tankered away for proper disposal. No direct discharge of groundwater from contaminated areas should be adopted. Prior to any excavation works within the potentially contaminated areas, the baseline groundwater quality in these areas should be reviewed based on the past relevant site investigation data and 	To minimise impact from groundwater from contaminated areas, contaminated site run-off/ wastewater from land decontamination	Contractor	All works area confirmed with land contamination	Construction phase	WPCO, EIAO- TM, TM-DSS, Guidance Note for Contaminated Land Assessment	N/A



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 any additional groundwater quality measurements to be performed with reference to Guidance Note for Contaminated Land Assessment and Remediation and the review results should be submitted to EPD for examination. If the review results indicated that the groundwater to be generated from the excavation works would be contaminated, this contaminated groundwater should be either properly treated or properly recharged into the ground in compliance with the requirements of the TM-DSS. If wastewater treatment is to be deployed for treating the contaminated groundwater, the wastewater treatment unit shall deploy suitable treatment processes (e.g. oil interceptor / activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (such as total petroleum hydrocarbon) to an undetectable range. All treated effluent from the wastewater treatment plant shall meet the requirements as stated in the TM-DSS and should be either discharged into the foul sewers or tankered away for proper disposal. If deployment of wastewater treatment is not feasible for handling the contaminated groundwater, groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in section 2.3 of TM-DSS. The baseline groundwater to be recharge wells, and submit a working plan to EPD for agreement. 						



	Concern to Address	Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
groundwater at the recharge well. Groundwater monitoring wells should be installed near the recharge points to monitor the effectiveness of the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products should be removed as necessary by installing the petrol interceptor. The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater.						
ement Implication (Construction Phase)						
 Recommendations for good site practices during the onstruction phase include: Nomination of approved personnel, such as a site manager, to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility; Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste management and chemical waste handling procedures; Provision of sufficient waste reception/ disposal points, and regular collection of waste; Adoption of appropriate measures to minimise windblown litter and dust during transportation of wastes in enclosed containers; Provision of regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; 	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	Waste Disposal Ordinance (WDO) and Public Cleansing and Prevention of Nuisances Regulation (Cap. 132BK)	Implemented
	points to monitor the effectiveness of the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products should be removed as necessary by installing the petrol interceptor. The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater. ement Implication (Construction Phase) ecommendations for good site practices during the onstruction phase include: Nomination of approved personnel, such as a site manager, to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility; Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste management and chemical waste handling procedures; Provision of sufficient waste reception/ disposal points, and regular collection of waste; Adoption of appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; Provision of regular cleaning and maintenance programme for drainage	points to monitor the effectiveness of the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products should be removed as necessary by installing the petrol interceptor. The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater. ement Implication (Construction Phase) ecommendations for good site practices during the onstruction phase include: Nomination of approved personnel, such as a site manager, to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility; Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste management and chemical waste handling procedures; Provision of sufficient waste reception/ disposal points, and regular collection of waste; Adoption of appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; Provision of regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; Adoption of a recording system for the amount of	points to monitor the effectiveness of the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products should be removed as necessary by installing the petrol interceptor. The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater. ement Implication (Construction Phase) ecommendations for good site practices during the onstruction phase include: Nomination of approved personnel, such as a site manager, to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility; Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste management and chemical waste handling procedures; Provision of sufficient waste reception/ disposal points, and regular collection of waste; Adoption of appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; Provision of regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; Adoption of a recording system for the amount of	points to monitor the effectiveness of the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products should be removed as necessary by installing the petrol interceptor. The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater. ecommendations for good site practices during the onstruction phase include: Nomination of approved personnel, such as a site manager, to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility; Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste management and chemical waste handling procedures; Provision of sufficient waste reception/ disposal points, and regular collection of waste; Adoption of appropriate measures to minimise windblown litter and dust during transporting wastes in enclosed containers; Provision of regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; Adoption of a recording system for the amount of	points to monitor the effectiveness of the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products should be removed as necessary by installing the petrol interceptor. The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater. ement Implication (Construction Phase) ecommendations for good site practices during the onstruction phase include: Nomination of approved personnel, such as a site manager, to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility; Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste management and chemical waste handling procedures; Provision of sufficient waste reception/ disposal points, and regular collection of waste; Adoption of appropriate measures to minimize windblown litter and dust during transporting wastes in enclosed containers; Provision of regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; Adoption of a recording system for the amount of	points to monitor the effectiveness of the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products should be removed as necessary by installing the petrol interceptor. The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater. ecommendations for good site practices during the onstruction phase include: Nomination of approved personnel, such as a site manager. to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility; Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste managerent and chemical waste handling procedures; Provision of sufficient waste reception / disposal points, and regular collection of waste; Adoption of appropriate measures to minimise windblown litter and dust during transporting wastes in enclosed containers; Provision of regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; Adoption of a recording system for the amount of



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	disposal sites); and						
	• Preparation of Waste Management Plan (WMP), as part of the Environmental Management Plan (EMP)						
S7.5.4	 Recommendations to achieve waste reduction are as follow: Segregate and store different types of construction related waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; 	To minimize waste generation	Contractor	All works areas	Construction phase	WDO	Implemented
	• Provide separate labelled bins to segregate recyclable waste such as aluminium cans from other general refuse generated by the work force, and to encourage collection by individual collectors;						
	• Recycle any unused chemicals or those with remaining functional capacity;						
	• Maximise the use of reusable steel formwork to reduce the amount of C&D materials;						
	• Adopt proper storage and site practices to minimise the potential for damage to, or contamination of construction materials;						
	• Plan the delivery and stock of construction materials carefully to minimise the amount of waste generated; and						
	• Minimize over ordering and wastage through careful planning during purchasing of construction materials.						
S7.5.6	To minimise the impact resulting from collection and transportation of C&D materials as far as practicable, C&D waste, such as wood, plastic, steel and other metals should be reused or recycled and, as a last resort, disposed to landfill. A suitable area should be designated within the site for temporary stockpiling of C&D materials and to facilitate the sorting process.	To minimise the disposal of C&D waste	Contractor	All works areas	Construction phase	WDO	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
S7.5.6	 Within the stockpile areas, the following measures should be taken to control potential environmental impacts or nuisance: Proper handling and storage of waste such as soil by means of covers and/or water spraying system to minimise the potential environmental impact and to prevent materials from wind-blown or being washed away; 	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	WDO	Implemented
	 Covering materials during heavy rainfall; Locating stockpiles to minimise potential visual impacts; Minimising land intake of stockpile areas as far as possible; 						
	• Adopting GPS or equivalent system for tracking and monitoring of all dump trucks engaged for the Project in recording their travel routings and parking locations to prohibit illegal dumping and landfilling of C&D materials; and						
	• Keeping record and analysis of data collected by GPS or equivalent system related to travel routings and parking locations of dump trucks engaged on site.						
S7.5.7 to S7.5.9	General refuse should be stored in enclosed bins or compaction units separate from C&D materials and chemical waste. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D materials and chemical wastes. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light materials.	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	WDO	Implemented
	The recyclable component of general refuse, such as aluminium cans, paper and cleansed plastic containers shall be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste shall						



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	be set up by the Contractor. The Contractor shall also be responsible for arranging recycling companies to collect these materials.						
	The Contractor shall carry out an education programme for workers in avoiding, reducing, reusing and recycling of materials generation. Posters and leaflets advising on the use of the bins shall also be provided in the sites as reminders.						
S7.5.10 to S7.5.12	If chemical wastes were to be produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer, and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	WDO	Implemented
	Appropriate containers with proper labels should be used for storage of chemical wastes. Chemical wastes should be collected and delivered to designated outlet by a licensed collector. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the CWTC, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.						
	Any unused chemicals or those with remaining functional capacity should be collected for reuse as far as practicable.						
	The sediment should be excavated, handled, transported and disposed of in a manner that would minimise adverse environmental impacts. For minimization of sediment disposal, beneficial reuse will be considered on site as far as practicable during the construction stage before the disposal of excavated sediment.	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	APCO WDO	N/A



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	Requirements of the Air Pollution Ordinance (Construction Dust) Regulation, where relevant, shall be adhered to during excavation, transportation and disposal of sediments.						
S7.5.15	In order to minimise the exposure to contaminated materials, workers shall, when necessary, wear appropriate personal protective equipment (PPE) when handling contaminated sediments. Adequate washing and cleaning facilities shall also be provided on site.	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	WDO	N/A
	Stockpiling of contaminated sediments shall be avoided as far as possible. If temporary stockpiling of contaminated sediments is unavoidable, the excavated sediment shall be covered by tarpaulin and the area shall be placed within earth bunds or sandbags to prevent leachate from entering the ground, nearby drains and/or surrounding water bodies. The stockpiles shall be completely paved or covered by linings in order to avoid contamination to underlying soil or groundwater. Separate and clearly defined areas shall be provided for stockpiling of contaminated and uncontaminated materials. Leachate, if any, shall be collected and discharged according to the Water Pollution Control Ordinance (WPCO).	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	WPCO	N/A
	In order to minimise the potential odour / dust emissions during excavation and transportation of the sediment, the excavated sediments shall be wetted during excavation / material handling and shall be properly covered when placed on trucks or barges. Loading of the excavated sediment to the barge shall be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding water.	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	WDO APCO	N/A



Recommended Mitigation Measures	Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
n						
imise environmental impacts arising from the g of potentially contaminated materials, the g environmental precautionary measures are ended to be utilised during the course of any site remediation: cavation profiles must be properly designed and ecuted with attention to the relevant requirements environment, health and safety; ablish and maintain a Health and Safety Plan with information below before commencement of the Instruction of works on work procedures, safe ctices, emergency duties, and applicable alations; Regularly scheduled meetings of the workers in ch the possible hazards, problems of the job, and ted safe practices are emphasized and discussed; Good housekeeping practices; and Availability of and instruction in the location, use maintenance of personal protective equipment. cavation shall be carried out during dry season as as possible to minimise contaminated runoff from traminated soils; oply of suitable clean backfill material (or treated l) after excavation; ckpiling site(s) shall be lined with impermeable eting and bunded. Stockpiles shall be fully covered impermeable sheeting to reduce dust emission. If	To control land remediation work	Contractor	Area identified with land contamination	construction works at the contaminated areas	Land Assessment	N/A
in gers cace eal i I contact in a contact in	mise environmental impacts arising from the of potentially contaminated materials, the g environmental precautionary measures are nded to be utilised during the course of any site remediation: avation profiles must be properly designed and cuted with attention to the relevant requirements environment, health and safety; blish and maintain a Health and Safety Plan with information below before commencement of the Instruction of works on work procedures, safe tices, emergency duties, and applicable lations; Regularly scheduled meetings of the workers in the the possible hazards, problems of the job, and ed safe practices are emphasized and discussed; Good housekeeping practices; and Availability of and instruction in the location, use maintenance of personal protective equipment. avation shall be carried out during dry season as as possible to minimise contaminated runoff from aminated soils; ply of suitable clean backfill material (or treated o after excavation; kpiling site(s) shall be lined with impermeable ting and bunded. Stockpiles shall be fully covered	n mise environmental impacts arising from the of potentially contaminated materials, the g environmental precautionary measures are nded to be utilised during the course of any site remediation: avation profiles must be properly designed and buted with attention to the relevant requirements environment, health and safety; blish and maintain a Health and Safety Plan with information below before commencement of the Instruction of works on work procedures, safe tices, emergency duties, and applicable lations; Regularly scheduled meetings of the workers in th the possible hazards, problems of the job, and ed safe practices are emphasized and discussed; Good housekeeping practices; and Availability of and instruction in the location, use maintenance of personal protective equipment. avation shall be carried out during dry season as as possible to minimise contaminated runoff from aminated soils; ply of suitable clean backfill material (or treated after excavation; kpiling site(s) shall be lined with impermeable ting and bunded. Stockpiles shall be fully covered mpermeable sheeting to reduce dust emission. If is not practicable due to frequent usage, regular ering shall be applied. However, watering shall be	h mise environmental impacts arising from the of potentially contaminated materials, the environmental precautionary measures are nded to be utilised during the course of any site remediation: To control land remediation work avation profiles must be properly designed and suted with attention to the relevant requirements environment, health and safety; Mise and maintain a Health and Safety Plan with information below before commencement of the lations; Regularly scheduled meetings of the workers in the possible hazards, problems of the job, and ed safe practices are emphasized and discussed; Good housekeeping practices; and Availability of and instruction in the location, use maintenance of personal protective equipment. avation shall be carried out during dry season as is possible to minimise contaminated runoff from aminated soils; ply of suitable clean backfill material (or treated after excavation; kpling site(s) shall be lined with impermeable tring and bunded. Stockpiles shall be fully covered mpermeable sheeting to reduce dust emission. If is not practicable due to frequent usage, regular tring shall be applied. However, watering shall be	A mise environmental impacts arising from the of potentially contaminated materials, the servironmental precautionary measures are neediation: To control land remediation work Area identified with land contamination mediation work avation profiles must be properly designed and ruted with attention to the relevant requirements invironment, health and Safety Plan with information below before commencement of the lations; To control land remediation: Area identified with attention to the relevant requirements invironment, health and Safety Plan with information below before commencement of the lations; Regularly scheduled meetings of the workers in the possible hazards, problems of the job, and ed safe practices are emphasized and discussed; Good housekeeping practices; and Availability of and instruction in the location, use maintenance of personal protective equipment. avation shall be carried out during dry season as is possible to minimise contaminated runoff from aminated soils; ply of suitable clean backfill material (or treated after excavation; kpiling site(s) shall be lined with impermeable ting and bunded. Stockpiles shall be fully covered mpermeable sheeting to reduce dust emission. If is not practicable due to frequent usage, regular ring shall be applied. However, watering shall be	1 mise environmental impacts arising from the of potentially contaminated materials, the s environmental precautionary measures are nded to be utilised during the course of any site remediation: To control land remediation work Area identified with land contamination construction works at the contaminated areas avation profiles must be properly designed and uted with attention to the relevant requirements environment, health and safety; Distance bilsh and maintain a Health and Safety Plan with information below before commencement of the lastons; Regularly scheduled meetings of the workers in th the possible hazards, problems of the job, and de safe practices are emphasized and discussed; Good housekceping practices; and Availability of and instruction in the location, use maintenance of personal protective equipment. avation shall be carried out during dry season as as possible to minimise contaminated runoff from aminated soils; py of suitable clean backfill material (or treated after excavation; kpiling site(s) shall be lined with impermeable ting and bunded. Stockpiles shall be fully covered mpermeable sheeting to reduce dust emission. If is not practicable due to frequent usage, regular ring shall be applied. However, watering shall be	h To control land of potentially contaminated materials, the genvironmental precautionary measures are nded to be utilised during the course of any site remediation: To control land remediation work Area identified with land contamination Prior to the commencement of for Contaminated and Remediation' areas avation profiles must be properly designed and turde with attention to the relevant requirements invironment, health and safety; bish and maintain at Health and Safety Plan with information below before commencement of the lations; Regularly scheduled meetings of the workers in th the possible hazards, problems of the job, and ed safe practices; and Availability of and instruction in the location, use maintenance of personal protective equipment, avation shall be carried out during dry season as is possible to minimise contaminated runoff from aminated soils; ply of suitable clean backfill material (or treated after excavation; kpling satu(s) shall be lined with impermeable ting and bunded. Stockfiles shall be fully covered mpermeable sheeting to reduce dust emission. If is not practicable due to frequent usage, regular ring shall be applied. However, watering shall be If a control to a control t



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 contaminated runoff; Vehicles containing any excavated materials shall be suitably covered to limit potential dust emissions or contaminated wastewater run-off, and truck bodies and tailgates shall be sealed to prevent any discharge during transport or during wet conditions; Speed control for the trucks carrying contaminated materials shall be enforced; Vehicle wheel and body washing facilities at the site exist points shall be established and used; and Pollution control measures for air emissions (e.g. from biopile blower and handling of cement), noise emissions (e.g. from blower or earthmoving equipment), and water discharges (e.g. runoff control from treatment facility) shall be implemented and complied with relevant regulations and guidelines. 						
Landscape	and Visual Impact (Construction Phase)						
S9.8.1	Trees unavoidably affected by the works should be transplanted as far as possible in accordance with DEVB TC(W) 7/2015 – Tree Preservation or LAO PN 7/2007 - Tree Preservation and Tree Removal Application for Building Development in Private Projects where applicable.	To transplant affected trees	Contractor	All works areas	Construction phase	DEVB TC(W) No. 7/2015 or LAO PN 7/2007 where applicable	N/A
S9.8.1	Control of night-time lighting glare.	To minimize the Landscape and visual	Contractor	All works areas	Construction phase	TM-EIAO	N/A
S9.8.1	Erection of decorative screen hoarding which should be compatible with the surrounding setting.	impact on surrounding setting	Contractor	All works areas	Construction phase	TM-EIAO	N/A
S9.8.1	Management of facilities on work sites by controlling the height and disposition/arrangement of all facilities on the works site to minimize visual impact to adjacent VSRs.	To minimize visual impact to adjacent VSRs.	Contractor	All works areas	Construction phase	-	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
S9.8.1	All hard and soft landscape areas disturbed temporarily	To minimize	Contractor	All works areas	Construction phase	-	To be
	during construction should be reinstated on like-to-like	the landscape			_		implemented
	basis, to the satisfaction of the relevant Government	impact on					
	Departments.	surrounding					
		setting					



Appendix L Monitoring Schedule of the Reporting Month



Consultancy Agreement No.NEX/1062 Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works - Advance Constuction Works Dust and Noise Monitoring Schedule in May 2023

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-May	2-May	3-May	4-May	5-May	6-May
				1-hr Dust Monitoring		
7-May	8-May	9-May	10-May	11-May	12-May	13-May
			1-hr Dust Monitoring			
14-May	15-May	16-May	17-May	18-May	19-May	20-May
		1-hr Dust Monitoring				
21-May	22-May	23-May	24-May	25-May	26-May	27-May
	1-hr Dust Monitoring					1-hr Dust Monitoring
28-May	29-May	30-May	31-May			



Appendix M Monitoring Schedule of the Coming Month



Consultancy Agreement No.NEX/1062 Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works - Advance Constuction Works Tentative Dust and Noise Monitoring Schedule in June 2023

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1-Jun	2-Jun	3-Jun
				1-hr Dust Monitoring		
4-Jun	5-Jun	6-Jun	7-Jun	8-Jun	9-Jun	10-Jun
			1-hr Dust Monitoring			
11-Jun	12-Jun	13-Jun	14-Jun	15-Jun	16-Jun	17-Jun
		1-hr Dust Monitoring				
18-Jun	19-Jun	20-Jun	21-Jun	22-Jun	23-Jun	24-Jun
	1-hr Dust Monitoring					1-hr Dust Monitoring
25-Jun	26-Jun	27-Jun	28-Jun	29-Jun	30-Jun	
					1-hr Dust Monitoring	

Remark: The monitoring schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather).

Appendix C

Monthly EM&A Report for May 2023 – Vehicular Access Bridge, Demolition of Paint Shop and Construction of EV Stabling Tracks Works Contract 1733



MTR Corporation Limited Siu Ho Wan Depot Property Development -Vehicular Access Bridge, Demolition of Paint Shop and Construction of EV Stabling Tracks Monthly EM&A Report (Period from 1 to 31 May 2023)

Prepared by

SGS Hong Kong Limited

MTR Corporation Limited

Issue and Revision Record

Revision	Description	Prepared by	Checked by	Approved by	Date
01	Submission	Various	Roy Hung AJ	Grace Fung , L	Jun 2023

Disclaimer

This document is issued by the Company under its General Conditions of Service accessible at <u>http://www.sgs.com/en/Terms-and-Conditions.aspx</u>. Attention is drawn to the limitation of liability, indemnification and jurisdiction issues defined therein.

Any holder of this document is advised that information contained hereon reflects the Company's findings at the time of its intervention only and within the limits of Client's instructions, if any. The Company's sole responsibility is to its Client and this document does not exonerate parties to a transaction from exercising all their rights and obligations under the transaction documents. Any unauthorized alteration, forgery or falsification of the content or appearance of this document is unlawful and offenders may be prosecuted to the fullest extent of the law.

	EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	3
SGS	Replanning Works – Contract 1733	Ref#	HKES230400003262
	Monthly EM&A Report	Rev.	01
			Jun-23

TABLE OF CONTENT

EXEC	UTIVE SUMMARY
1.	PROJECT INFORMATION
2.	ENVIRONMENTAL STATUS8
3.	AIR QUALITY MONITORING 10
4.	WASTE MANAGEMENT 12
5.	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS 13
6.	EM&A SITE INSPECTION
7.	FUTURE KEY ISSUES
8.	CONCLUSION AND RECOMMENDATION 17
APPE	NDIX A – CONSTRUCTION PROGRAMME
APPE	NDIX B – PROJECT ORGANIZATION CHART
APPE	NDIX C – ALIGNMENT AND WORKS AREA FOR CONTRACT NO. 1733
APPE	NDIX D - LOCATION PLAN OF MONITORING STATION
APPE	NDIX E - CALIBRATION CERTIFICATES
APPE	NDIX F – MONITORING DATA
APPE	NDIX G – WASTE FLOW TABLE
APPE	NDIX H - COMPLAINT HANDLING PROCEDURE
APPE	NDIX I - EVENT-ACTION PLAN
APPE	NDIX J - STATISTICS ON COMPLAINT, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTION
APPE	NDIX K - ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE (EMIS)
APPE	NDIX L - MONITORING SCHEDULE OF THE REPORTING MONTH
APPE	NDIX M - MONITORING SCHEDULE OF THE COMING MONTH



EXECUTIVE SUMMARY

SGS Hong Kong Limited. ("SGS") has been commissioned by the Build King Civil Engineering Limited, to undertake the Environmental Team (ET) services to carry out environmental monitoring and audit (EM&A) for Vehicular Access Bridge, Demolition of Paint Shop and Construction of EV Stabling Tracks (hereafter referred to as the "Project").

This is the 14th monthly EM&A report for the project submitted under Condition 3.4 of the Environmental Permit (No. EP-588/2021). This report summarises the findings on EM&A during the period from 1 to 31 May 2023.

Exceedance of Action and Limit Levels

The summary of measured 1-hour TSP level is presented in Section 3.

No exceedance of Action or Limit Levels for 1-hour TSP levels were recorded in the Reporting Period.

Waste Management

Details of waste management are presented in Section 4.

Record of Complaints

There was no record of complaints received in the Reporting Period.

Record of Notification of Summons and Successful Prosecutions

There were no record of notification of summons and successful prosecution in the Reporting Period.

Reporting Changes

There are no reporting changes.

Site inspection

Weekly environmental site inspections were conducted during the reporting period. A joint site inspection with the IEC was carried out on 8 May 2023. Non-compliance was not observed. Observation and recommendation were reported during the site inspection. Items are rectified accordingly in the reporting period. The environmental performance of the Project was therefore considered satisfactory.

Future Key Issues

- Excavation
- Substructure
- UU Diversion
- EV Tracks Formation and Track installation



- Construction of vehicular access bridge
- Grout curtain works
- Chain Link Fence works



1. **PROJECT INFORMATION**

The Project involves the construction of vehicular access bridge, demolition of paint shop and construction of engineering vehicle (EV) stabling tracks.

The (AEIAR-214/2017) "Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works" Environmental Impact Assessment Report was approved with conditions by the Environmental Protection Department (EPD) on 29 Nov 2017. The latest Environmental Permit (No. EP-588/2021) was issued by the EPD on 22 March 2021.

SGS Hong Kong Limited (SGS) has been commissioned by Build King Civil Engineering Limited to undertake the Environmental Team (ET) services to carry out environmental monitoring and audit for this project.

The Project covers the following construction activities:

- Site clearance & hoarding /UU/ Cable Trenches
- Paint shop demolition
- Excavation
- Substructure
- Backfilling
- Superstructure
- EV Tracks Formation and Track installation

The construction programme is presented in Appendix A

A summary of the major construction activities undertaken in this reporting period (from 1 to 31 May 2023) is shown in below:

- Excavation
- Substructure
- UU Diversion
- EV Tracks Formation and Track installation
- Construction of vehicular access bridge
- Grout curtain works
- Chain Link Fence works



The project organizational chart specifying management structure and contact details are shown in **Appendix B**.

A summary of the valid permits, licenses, and /or notifications on environmental protection for this Project is presented in **Table 1.1**.

Type of Permit/ License	Permit No. / Account No.	Valid From	Expiry Date	Status
Environmental Permit	EP-588/2021	22 Mar 2021	N/A	Valid
Wastewater Discharge License	WT00041829- 2022	31 Aug 2022	31 Aug 2027	Valid
Notification of Construction Works under the Air Pollution Control (Construction Dust) Regulation	Ref.: 477410	N/A	N/A	Notification submitted on 3 Mar 2022
Chemical Waste Producer Registration	WPN5213-961- B2653-01	15 Feb 2022	N/A	Valid
Billing Account for Disposal of Construction Waste	7043460	18 Mar 2022	N/A	Valid
Construction Noise Permit	GW-RS0484-22	22 Jun 2022	15 Dec 2022	Suspended on 16 Dec 2022
	GW-RS1036-22	16 Dec 2022	15 June 2023	Valid

Table 1.1 Summary of Status of Required Submission for EP-588/2021 for the Project



2. ENVIRONMENTAL STATUS

Environmental permit (EP) conditions under the EIAO, submission status under the EP and implementation status of mitigation measures had been reviewed and implemented on schedule. The status of required submissions under the EP (No. EP-588/2021) as of the reporting period for the Project are summarised in **Table 2.1**.

EP Condition	Submission	Submission Date
1.12	Commencement Date of Construction	11 Jun 2021 (1st submission)
		12 Jul 2021 (2nd submission)
		12 Aug 2021 (3rd submission)
2.7	Construction Works Phasing Schedule	1 Nov 2021 (1st submission)
		20 Dec 2021 (2nd submission)
		29 Dec 2021 (Deposited)
2.8	Environmental Permit Submission Schedule	12 Aug 2021
		10 Sep 2021 (Deposited)
2.9	Management Organization	1 Nov 2021 (1st Submission)
		20 Dec 2021 (2nd Submission)
		21 Mar 2022 (3rd Submission)
		9 Aug 2022 (4th Submission)
		16 Nov 2022 (5th Submission)
2.10	Construction Noise Mitigation Plan	1 Nov 2021 (1st submission for advanced work)
		20 Dec 2021 (2nd submission for advanced work)
		28 Dec 2021 (3rd submission for advanced work)



		 30 Dec 2022 (1st submission for Phase 1 work) 29 Mar 2023 (2nd submission for Phase 1 work) 18 May 2023 (3rd submission for Phase 1 work)
2.11	Noise Mitigation Plan	31 Mar 2023 (1st submission)
2.13	Waste Management Plan	1 Nov 2021 (1st submission) 20 Dec 2021 (2nd submission) 28 Dec 2021 (Deposited)
2.15	Landscape and Visual Plan	27 April 2023 (1st submission)
3.3	Baseline Monitoring Report	1 Nov 2021 16 Nov 2021 (Deposited)
3.4	Monthly Monitoring Report (Apr 2023)	To be submitted within 10 working days after the end of the reporting month
4.2	Dedicated Internet Website	12 Jan 2022

The drawings showing the project layout and the location of the monitoring station are attached in **Appendix C** and **Appendix D**, respectively. A summary of the monitoring location is shown in **Table 2.2**.

Table 2.2 Summary of th	e location of the monitoring station
-------------------------	--------------------------------------

Air Sensitive Receiver (ASR) ID No. in EIA	Monitoring Station	Description		
A2	DM1	Siu Ho Wan Government Maintenance Depot		



3. AIR QUALITY MONITORING

MONITORING REQUIREMENTS, FREQUENCY AND DURATION

The impact monitoring had been carried out in accordance with Section 2.6 of the approved EM&A Manual, with sampling frequency of at least 3 times in every 6 days undertaken, to determine the 1-hour total suspended particulates (TSP) levels at the monitoring locations in the reporting period.

General meteorological conditions (wind speed, direction and precipitation) and notes regarding any significant adjacent dust producing sources had also been recorded throughout the impact monitoring period.

Monitoring Equipment

Portable direct reading dust meter was used to carry out the 1-hour TSP monitoring. Portable direct reading dust meters used in this monitoring were proven to the IEC to be capable of achieving comparable result as that of the HVS and, thus, were used for sampling. The equipment used for 1-hour TSP measurement during the reporting month are summarised in **Table 3.1**.

Measuring	Monitoring		Brand		Model No.	Calibration		
Parameter	Equipment		Equipment		er Equipment			Date
1-hour TSP	Portable	direct	Sibata	Digital	A.005.16a	4 April 2023		
	reading dust	meter	Dust	Monitor				
	(1-hour TSP)		(Model No. LD-					
			3)					

Table 3.1 Construction Dust Monitoring Equipment

The portable direct reading dust meter was calibrated at 1-year interval against a High Volume Sampler, TE-5170. Copies of calibration certificates of the portable direct reading dust meter are presented in **Appendix E**.

Field Monitoring Methodology

The 1-hour TSP measurement followed manufacturer's instruction manual. Before initiating a measurement, zeroing the Portable direct reading dust meter was carried out to ensure maximum accuracy of concentration measurements.

The 1-hour TSP was sampled by drawing air into the portable direct reading dust meter where particular concentrations were measured instantaneously with an in-built silicon detector sensing light scattered by the particulates in the sampled air. Continuous TSP levels were indicated and logged by a built-in data logger compatible with Windows based program to facilitate data collection, analysis and reporting.



Monitoring Location

Location of the designated dust monitoring station is described in Table 3.2.

Table 3.2 Location of the designated dust monitoring station

Monitoring Station ID	Dust Monitoring Station		
DM1	Siu Ho Wan Government Maintenance Depot		

Result Summary

Dust impact monitoring was carried out at DM1 on 4, 10, 16, 22 and 27 May 2023 during the reporting month (**Appendix L**). According to our field observations, the major dust sources identified included vehicular emissions from North Lantau Highway and Cheung Tung Road. Gentle wind was recorded throughout the monitoring period, with gentle to strong wind recorded occasionally.

The results for 1 - hour TSP are summarized in **Table 3.3**. The measurement data is presented in **Appendix F**

Table 3.3 Summary of 1-hour TSP Monitoring Results

Monitoring Location	Range (µg/m3)	Action Level	Limit Level	No. of
		(µg/m3)	(µg/m3)	Exceedances
DM1	58.9 - 63.3	294.7	500	0



4. WASTE MANAGEMENT

The waste generated from this Project includes inert C&D materials, and non-inert C&D materials. Noninert C&D materials are made up of general refuse, vegetative wastes and recyclable wastes such as plastics and paper/ cardboard packaging waste. Metals materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarized in Table 4.1. Details of cumulative waste management data are presented as a waste flow table in **Appendix G**.

Table 4.1 Quantities of waste generated from the Project

Month	Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of C&D Materials Generated Monthly					
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposal as Public Fill	Imported Fill	Metals	Paper / Cardboard Packaging	Plastics (See note 3)	Chemical Waste	Other, e.g. general refuse
	[in Tonne]	[in Tonne]	[in Tonne]	[in Tonne]	[in Tonne]	[in Tonne]	[in Tonne]	[in kg]	[in kg]	[in kg]	[in Tonne]
Мау	307.51	0.00	0.00	0.00	307.51	0.00	0.00	0.00	0.00	0.00	30.13

All dump trucks for C&D materials transportation and disposal are equipped with Global Positioning System (GPS) for real time tracking and monitoring their travel routings and parking locations in order to avoid illegal dumping or landfilling of C&D materials.

The GPS data including travel routings of dump trucks was reviewed by the ET and IEC, and no illegal dumping activities were suspected.



5. SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS

The Environmental Complaint Handling Procedure is shown in **Appendix H**.

Should non-compliance of the criteria occur, action in accordance with the Event and Action Plan in **Appendix I** shall be carried out.

No exceedance of the Action and Limit Levels of 1-hour TSP was recorded during the reporting month.

No complaint or non-compliance was reported in the reporting month.

No notification of summons and prosecution was received in the reporting period.

Statistics on complaints, notifications of summons and successful prosecutions are summarized in **Appendix J**.




6. EM&A SITE INSPECTION

Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, four (5) site inspections were carried out on 2, 8, 15, 22 and 29 May 2023. One joint site inspection with the IEC also undertaken on 8 May 2023 with engineer, IEC, contractor and contractor's ET. No observations and reminders were reported during the weekly site inspection. Key observations during the site inspections are summarized in **Table 6.1**.

Table 6.1 Site Observations

Date	Observation or Reminder	Follow-up Status
2 May 2023	Observation 1: The contractor was reminded to conduct water spraying for exposed soil regularly. (Target date: 3 May 2023)	Exposed Soil have been sprayed with water. (Item closed on 3 May 2023)
8 May 2023	Observation 1: It is observed that there is oil stain on the ground near W2, the contractor was reminded to remove oil stain. (Target date: 8 May 2023) Observation 2: It is observed that there is no cover for the stockpile at W3, the contractor was reminded to conduct water spraying for exposed soil regularly. (Target date: 12 May 2023)	Spoiled Soil was absorbed by chemical absorbent materials. (Item closed on 8 May 2023) Exposed Soil have been sprayed with water. (Item closed on 10 May 2023)
15 May 2023	No particular findings during inspection.	N/A
22 May 2023	No particular findings during inspection.	N/A
29 May 2023	Observation 1: The contractor was reminded to conduct water spraying on exposed site surfaces and unpaved roads for dust suppression. (Target date: 30 May 2023)	Exposed site surfaces and unpaved roads have been water sprayed for dust suppression (Item closed on 30 May 2023) The NRMM Label is attached
	Observation 2: The contractor was reminded to affix NRMM label on the excavator. (Target	on the excavator. (Item closed on 30 May 2023)



date: 30 May 2023)

According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents are implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix K**.



7. FUTURE KEY ISSUES

Work to be undertaken in the next reporting month are:

- Excavation
- Substructure
- UU Diversion
- EV Tracks Formation and Track installation
- Construction of vehicular access bridge
- Grout curtain works
- Chain Link Fence works

The tentative schedule of regular 1-hour TSP monitoring in the next reporting period is presented in **Appendix M**.



8. CONCLUSION AND RECOMMENDATION

This 14th monthly EM&A Report presents the EM&A works undertaken during the period from 1 May to 31 May 2023 in accordance with the EM&A Manual and the requirement under EP-588/2021.

Air quality (including 1-hour TSP) impact monitoring was carried out in the reporting period. No exceedance of the Action and Limit Levels was recorded for air quality impact monitoring during the reporting period.

Weekly environmental site inspections were conducted during the reporting period. A joint site inspection with the IEC was carried out on 8 May 2023. Non-compliance was not observed. Observation and recommendation were reported during the site inspection. Items are rectified accordingly in the reporting period. The environmental performance of the Project was therefore considered satisfactory.

No complaint or non-compliance was reported in the reporting month.

No notification of summons or prosecution was received in the reporting month.

The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

The proposed mitigation measures were properly implemented and were considered effective and efficient in pollution control.



EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	A-1
Replanning Works – Contract 1733	Ref#	HKES2304000032
Monthly EM&A Report	Rev.	01
	Date	Jun-23

APPENDIX A – CONSTRUCTION PROGRAMME




Construction Activities						2022	2										2023					
Constituction Activities	J	F	М	Α	М	J	JA	4 8	S 0	Ν	D	J	F	М	Α	M ,	JJ	Α	S	0	N)
Contract 1733 - Vehicular Access Bridge, Demolition of Paint Shop and Construction of EV Stabling Tracks																						
Site Clerance & Hoarding / UU / Cable Trenches																				\Box		
Paint Shop Demolition																						
Excavation (Soil)																						
Substructure (footing, pile caps, columns, abutments)																						
Backfilling																						
Superstructure (Vehicular Bridge Spans)																						
EV Tracks - Formation and Track Installation																						



EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	B-1
Replanning Works – Contract 1733	Ref#	HKES2304000 03262
Monthly EM&A Report		01
	Date	Jun-23

APPENDIX B – PROJECT ORGANIZATION CHART

	ED 500/0024 - Six U.S. Was Station and Six U.S. Was Depart Depleming Works - Contract 4722	Page	B-2
	EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works – Contract 1733	Ref#	HKES2304000 03262
909	Monthly EM&A Report	Rev.	01
		Date	Jun-23

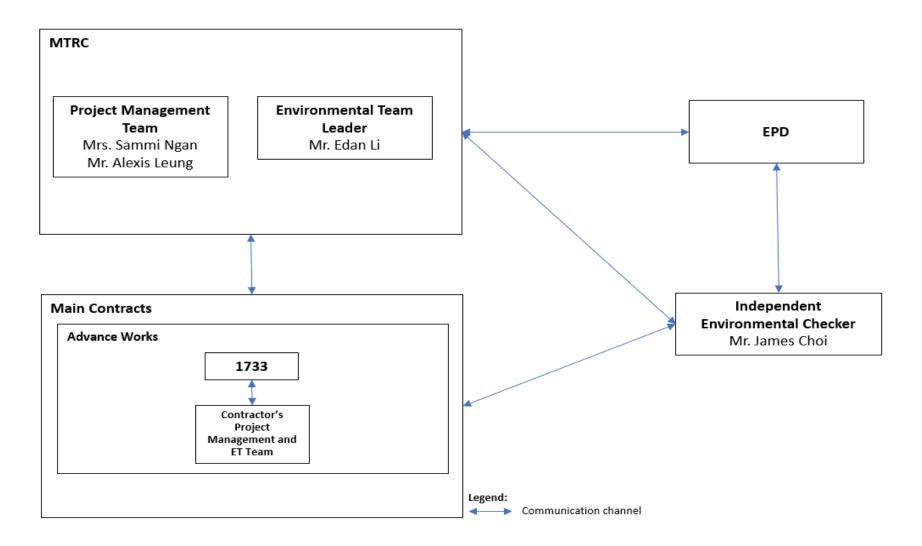



ED 500/0004 - Oix Ha Way Otation and Oix Ha Way Danat Danlandian Washa - Oantaast 4700	Page	B-3
EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works – Contract 1733	Ref#	HKES2304000 03262
Monthly EM&A Report	Rev.	01
	Date	Jun-23

MTR's Contact:

MTRC - Project Management Team		
Position	Name	Telephone
Chief Construction Manager - OYB	Mrs. Sammi Ngan	2208 3753
Senior Construction Manager - Civil	Mr. Alexis Leung	2208 3968

MTRC - Environmental Team		
Position	Name	Telephone
Environmental Team Leader	Mr. Edan Li	2688 1179
Environmental Team Member	Mr. Cyrus Lau	2688 1585

ANewR Consulting Limited - IEC								
Position	Name	Telephone						
Independent Environmental Checker	Mr. James Choi	2618 2836						

Contractor's Contact


Main Works Contract	Description	Contractor	Position	Name	Telephone
			Project Manager	Andy Yu	9648 4896
	Vehicular access bridge, demolition of paint shop and	Build King Civil	Environmental Manager	Louisa Fung	9271 5370
1733	construction of engineering	Engineering	Environmental Officer	Jason Cheng	6158 2117
	vehicle stabling tracks	Ltd	Environmental Team Leader	Roy Hung	2204 8305



EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	C-1
Replanning Works – Contract 1733	Ref#	HKES230400003262
Monthly EM&A Report	Rev.	01
	Date	Jun-23

APPENDIX C - ALIGNMENT AND WORKS AREA FOR CONTRACT NO. 1733

ED 599/2021 Sin He Was Station and Sin He Was Danet Danlanning Works Contract 1722	Page	C-2
EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works – Contract 1733	Ref#	HKES230400003262
Monthly EM&A Report	Rev.	01
		Jun-23

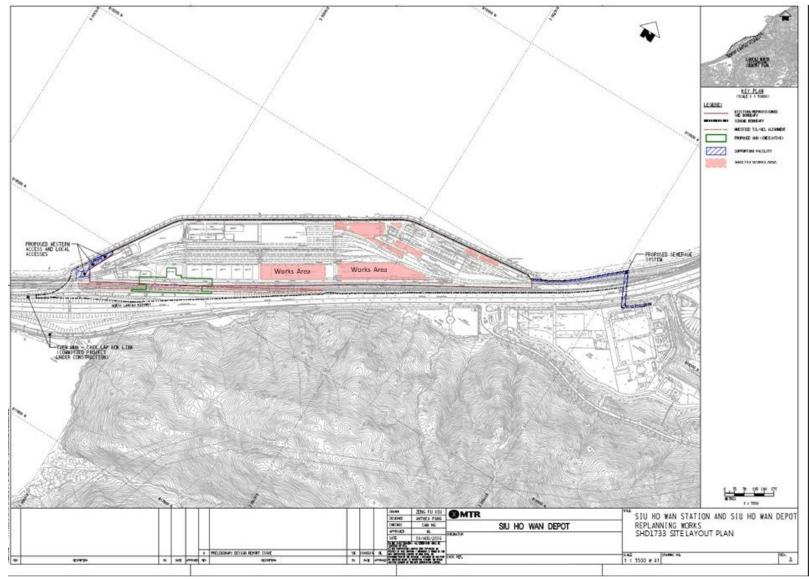




EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	D-1
Replanning Works – Contract 1733	Ref#	HKES230400003262
Monthly EM&A Report	Rev.	01
	Date	Jun-23

APPENDIX D - LOCATION PLAN OF AIR QUALITY MONITORING STATION

ED 500/2024 Six Us Was Station and Six Us Was Depart Deplemains Works - Contract 1722	Page	D-2
EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works – Contract 1733	Ref#	HKES230400003262
Monthly EM&A Report	Rev.	01
	Date	Jun-23

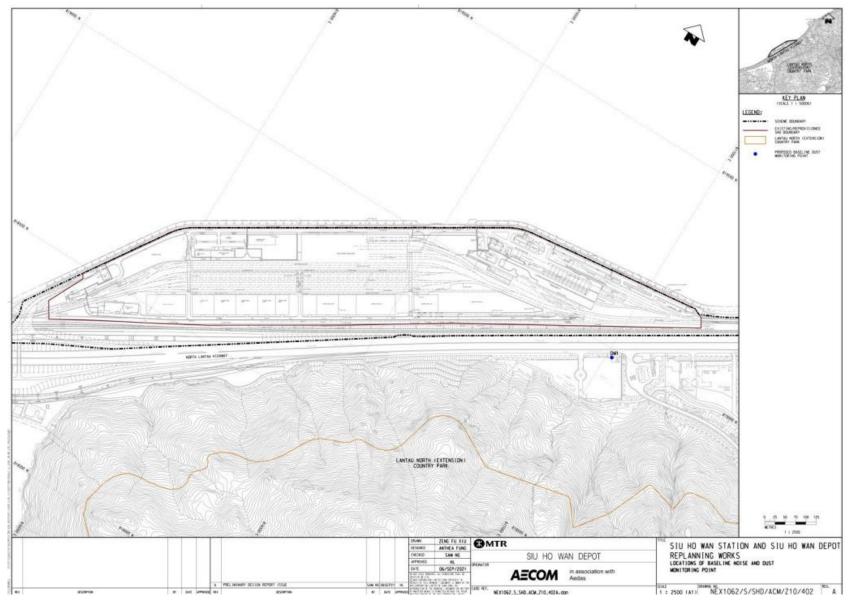



APPENDIX E - CALIBRATION CERTIFICATES (AIR QUALITY MONITORING EQUIPMENT)



EQUIPMENT CALIBRATION RECORD

Type:	Laser Dust Monitor	
Manufacturer/Brand:	SIBATA	
Model No.:	LD-3B	
Equipment No.:	A.005.16a	-
Sensitivity Adjustment Scale Setting:	521 CPM	
Operator:	WS CHAN	
Standard Equimment		
Equipment:	High Volume Sampler	
Venue:	Pedestrian Plaza	
Model No.:	TE-5170	
Serial No.:	10273	-
Last Calibration Date:	4-Apr-23	•

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): Sensitivity Adjustment Scale Setting (After Calibration):

521 СРМ 521 CPM

Hour	Date	Time	Ambient Condition		Concentration (1)	Total Count(2)	Count/
	(dd/mm/yy)		Temp (°C) R.H.(%)		(mg/m3)		Minute(3)
					Y-axis		X-axis
1	26/04/23	9:00-10:00	23.5	65	0.0490	1860	31.00
2	26/04/23	10:00-11:00	23.5	65	0.0500	1940	32.33
3	26/04/23	11:00-12:00	23.5	65	0.0520	2020	33.67
4	26/04/23	12:00-13:00	23.5	65	0.0540	2150	35.83
Note:	Note: ① Monitoring data was measured by High Volume Sampler						

1 Monitoring data was measured by High Volume Sampler

Total Count was logged by Laser Dust Monitor

③ Count/minute was calculated by (Total Count/60)

By Linear Regression of Y on X

Slope (K-factor):	0.0015
Correlation coefficient:	0.9997
Validity of Calibration Record:	26-Apr-24
validity of Calibration Record:	20-Apr-24

26-Apr-24

Remarks:

QC Reviewer:

Y.W. Fung

Signature:

Date: 28-Apr-23




EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	F-1
Replanning Works – Contract 1733	Ref#	HKES230400003262
Monthly EM&A Report	Rev.	01
	Date	Jun-23

APPENDIX F – MONITORING DATA (AIR QUALITY MONITORING)



The Summary of 1-hour TSP Concentration ($\mu g/m^3$) at Location DM1

	Start	1st Hour	2nd Hour	3rd Hour	Action Level	Limit Level	Exceedance
	Time	Conc.	Conc.	Conc.	Conc.	Conc.	
Date	(hh:mm)	(µg/m³)	(µg/m³)	(µg/m³)	(µg/m³)	(µg/m³)	(Y/N)
4-May-23	11:05	60.2	62.8	63.3			N
10-May-23	11:00	60.6	61.8	60.2			N
16-May-23	13:45	58.9	61.1	62.0	294.7	500	N
22-May-23	10:50	59.5	60.9	61.1			N
27-May-23	11:10	62.2	61.3	62.4			N
			Average	61.2			
			Min	58.9			
			Max	63.3			

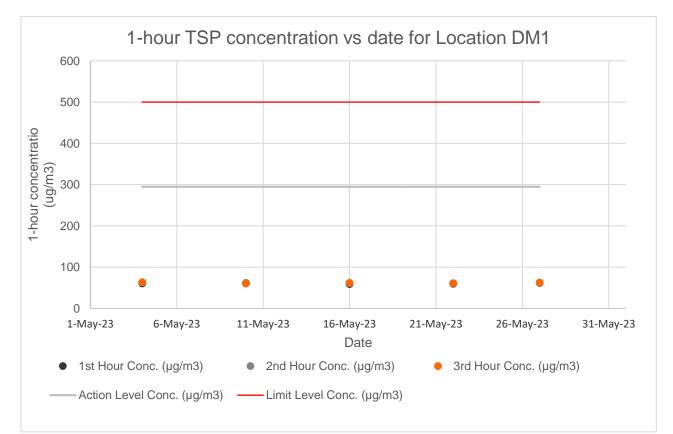



EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	G-1
Replanning Works – Contract 1733	Ref#	HKES230400003262
Monthly EM&A Report	Rev.	01
	Date	Jun-23

APPENDIX G – WASTE FLOW TABLE



Monthly Summary Waste Flow Table for 2023 Year

	Actual Quantities of Inert C&D Materials Generated Monthly Actual Quantities of <u>Non-inert</u> C&D Materials Generated Monthly						erials				
Month	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposal as Public Fill	Imported Fill	Metals	Paper / Cardboard Packaging	Plastics	Chemical Waste	Other, e.g. general refuse
	[in Tonne]	[in Tonne]	[in Tonne]	[in Tonne]	[in Tonne]	[in Tonne]	[in Tonne]	[in kg]	[in kg]	[in kg]	[in Tonne]
Jan	387.77	0.00	0.00	0.00	387.77	0.00	10.40	0.00	0.00	0.00	6.92
Feb	2012.65	0.00	0.00	0.00	2012.65	0.00	18.70	0.00	0.00	0.00	11.31
Mar	526.54	0.00	0.00	0.00	526.54	0.00	0.00	0.00	0.00	0.00	20.98
Apr	222.70	0.00	0.00	0.00	222.70	0.00	0.00	0.00	0.00	0.00	6.29
Мау	307.51	0.00	0.00	0.00	307.51	0.00	0.00	0.00	0.00	0.00	30.13
June											
SUB- TOTAL	3457.17	0.00	0.00	0.00	3457.17	0.00	29.10	0.00	0.00	0.00	75.63
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
TOTAL	3457.17	0.00	0.00	0.00	3457.17	0.00	29.10	0.00	0.00	0.00	75.63


¹ full loaded dumping truck is assumed equivalent to 6.5 m3 by volume from Archsd D/OL03/09.002


Note: Plastics refer to plastic bottles / containers, plastic sheets / foam from packaging material



EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	H-1
Replanning Works – Contract 1733	Ref#	HKES230400003262
Monthly EM&A Report	Rev.	01
	Date	Jun-23

APPENDIX H - COMPLAINT HANDLING PROCEDURE



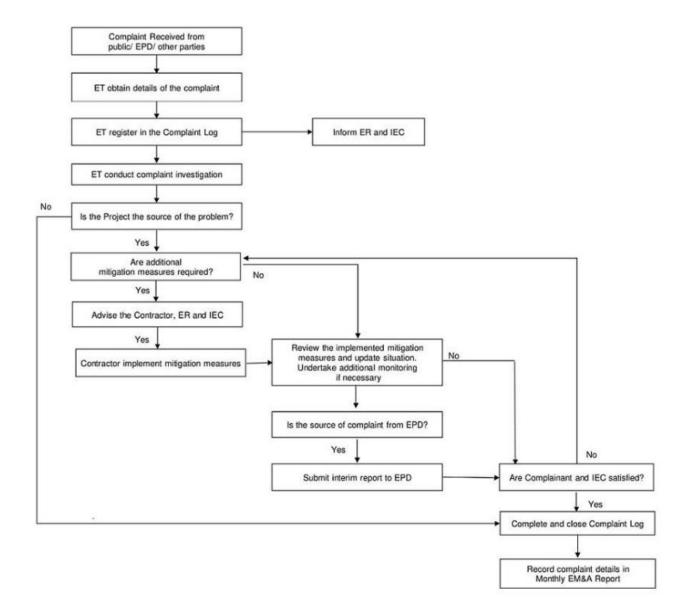



EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	I-1
Replanning Works – Contract 1733	Ref#	HKES230400003262
Monthly EM&A Report	Rev.	01
	Date	Jun-23

APPENDIX I - EVENT-ACTION PLAN (AIR QUALITY MONITORING)"



Monthly	EM&A	Report
---------	------	--------

EVENT	ACTION			
EVENT	ET	IEC	ER	CONTRACTOR
ACTION LEVEL				
Exceedance for one sample	 Repeat measurement to confirm findings; If exceedance is confirmed, inform the Contractor, IEC and ER; Identify source(s), investigate the causes of exceedance and propose remedial measures; and Increase monitoring frequency. 	 Check monitoring data submitted by the ET; Check Contractor's working method; and Discuss with ET, ER and Contractor on possible remedial measures Review and advise the ET and ER on the effectiveness of the proposed remedial measures. 	 Confirm receipt of notification of exceedance in writing. 	 Identify source(s), investigate the causes of exceedance and propose remedial measures; Implement remedial measures; and Amend working methods agreed with the ER as appropriate.
Exceedance for two or more consecutive samples	 Repeat measurements to confirm findings; If exceedance is confirmed, inform Contractor, IEC and ER; Identify source(s), investigate the causes of exceedance and propose remedial measures; Increase monitoring frequency to daily; Advise the Contractor and ER on the effectiveness of the proposed remedial measures; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with Contractor, IEC and ER to 	 Check monitoring data submitted by the ET; Check Contractor's working method; and Discuss with ET, ER and Contractor on possible remedial measures; Review and advise the ET and ER on the effectiveness of the proposed remedial measures; and Supervise Implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; In consultation with the ET and IEC agree with the Contractor on the remedial measures to be implemented; and Supervise implementation of remedial measures 	 Identify source(s) and investigate the causes of exceedance; Submit proposals for remedial measures to the ER, ET and IEC within three working days of notification for agreement; Implement the agreed proposals; and Amend proposal as appropriate.



Monthly EM&A Repor	t
--------------------	---

	ACTION			
EVENT	ET discuss the remedial measures to be taken; and 8. If exceedance stops, cease additional monitoring.	IEC	ER	CONTRACTOR
LIMIT LEVEL				
Exceedance for one sample	 Repeat measurement to confirm findings; If exceedance is confirmed, inform the Contractor, IEC, EPD and ER; Identify source(s), investigate the causes of exceedance and propose remedial; Increase monitoring frequency to daily; and Discuss with the ER, IEC and Contractor on the remedial measures and assess effectiveness. 	 Check monitoring data submitted by the ET; Check Contractor's working method; Discuss with the ET, ER and Contractor on possible remedial measures; Review and advise the ET and ER on the effectiveness of the proposed remedial measures; and Supervise implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Review and agree on the remedial measures proposed by the Contractor; and Ensure remedial measures properly implemented. 	 Identify source(s) and investigate the causes of exceedance; Take immediate action to avoid further exceedance; Submit proposals for remedial measures to ER, ET and IEC within three working days of notification for agreement; Implement the agreed proposals; and Amend proposal if appropriate.
Exceedance for two or more consecutive samples	 Repeat measurement to confirm findings; If exceedance is confirmed, inform IEC, ER, Contractor and EPD; Identify source(s), investigate the causes of exceedance and propose remedial measures; 	 Check monitoring data submitted by the ET; Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their 	 Confirm receipt of notification of exceedance in writing; In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures; and 	 Identify source(s) and investigate the causes of exceedance; Take immediate action to avoid further exceedance; Submit proposals for remedial measures to the ER, IEC and ET within three working days of notification for agreement;



Monthly EM&A Report

		TION		
EVENT	ET	IEC	ER	CONTRACTOR
	 Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and If exceedance stops, cease additional monitoring. 	effectiveness and advise the ER accordingly; and 4. Supervise the implementation of remedial measures.	 If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Implement the agreed proposals; Revise and resubmit proposals if problem still not under control; and Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Note: ET – Environmental Team; ER – Engineer's Representative; IEC – Independent Environmental Checker



APPENDIX J - STATISTICS ON COMPLAINT, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTION



Statistic Summary of Exceedance

Air Quality							
Location	Location Action Level Limit Level Total						
DM1	0	0	0				

Statistical Summary of Environmental Complaint

	Environmental Complaint Statistics						
Reporting Period	Frequency	Cumulative	Complaint Nature				
1 May 2023 – 31 May 2023	0	0	0				

Statistical Summary of Environmental Non-compliance

	Environr	mental Non-compliance \$	Statistics	
Reporting Period	Frequency	Cumulative	Complaint Nature	
1 May 2023 – 31 May 2023	0	0	0	

Statistical Summary of Environmental Summons

	Envir	onmental Summons Stat	tistics
Reporting Period	Frequency	Cumulative	Complaint Nature
1 May 2023 – 31 May 2023	0	0	0

	EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	J-3
SGS	Replanning Works – Contract 1733	Ref#	HKES230400003262
	Monthly EM&A Report	Rev.	01
		Date	Jun-23

Statistical Summary of Environmental Prosecution

Dementing Deviad	Enviro	nmental Prosecution Sta	atistics	
Reporting Period	Frequency	Cumulative	Complaint Nature	
1 May 2023 – 31 May 2023	0	0	0	



APPENDIX K - ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE (EMIS)



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
Air Quality	(Construction Phase)						
S3.8.1	Watering once per hour on active works areas, exposed areas and unpaved haul roads during working hours.	To minimize dust impacts	Contractor	All works area	Construction phase	Air Pollution Control Ordinance (APCO)	Implemented
\$3.8.9	 Implementation of dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices should be carried out to further minimize construction dust impact. Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. Use of frequent watering for particularly dusty construction areas and areas close to ASRs. Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines. Open stockpiles should be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations. Establishment and use of vehicle wheel and body washing facilities at the exit points of the site. Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading points, 		Contractor	All works area	Construction phase	Air Pollution Control Ordinance (APCO)	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods.						
	• Imposition of speed controls for vehicles on unpaved site roads. 8 kilometres per hour is the recommended limit.						
	• Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs.						
	• Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.						
	• Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed.						
	• Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system.						
Noise Impa	act (Construction Phase)	I		1		I	
S4.5.16	Implement the following good site practices as far as practicable: • Only well-maintained plant should be operated on-site,	To minimise impacts to surrounding habitats	Contractor	All works area	Construction phase	TM-EIAO	Implemented
	and plant should be serviced regularly during the						



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	construction program;						
	 Silencers or mufflers on construction equipment should be utilised and should be properly maintained during the construction program; 						
	 Mobile plant, is any, should be sited as far from NSRs as possible; 						
	 Machine and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; 						
	 Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and 						
	 Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities 						
S4.5.17	Adopting quiet PME is recommended. The type of quiet PME adopted in this assessment is for reference only. The contractors may adopt alternative quiet PME as long as it can be demonstrated that they would not result in construction noise impacts worse than those predicted in this assessment.	To reduce impact to affected NSRs	Contractor	All works area	Construction phase	TM-EIAO	Implemented
S4.5.19	Use of noise barriers and noise enclosures to provide screening for construction plant where recommended.	To reduce impact to affected NSRs	Contractor	All works area	Construction phase	TM-EIAO	N/A
Water Qual	ity Impact (Construction Phase)		1	<u> </u>	1	1	I
S5.8.4	Surface and road run-off from construction sites should be discharged into storm drains via adequately designed	To minimise impact from	Contractor	All works area	Construction phase	Water Pollution Control	



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	sand/silt removal facilities such as sand traps, silt traps and sedimentation basins. Channels or earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Perimeter channels should be provided on site boundaries where necessary to intercept storm run-off from outside the site so that it will not wash across the site. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.					Ordinance (WPCO), Technical Memorandum on EIA Ordinance (EIAO-TM), ProPECC PN 1/94, Technical Memorandum on Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters (TM-DSS)	implemented
\$5.8.5	Silt removal facilities, channels and manholes should be maintained, and the deposited silt and grit should be removed regularly, at the onset of and after each rainstorm to prevent local flooding. Any practical options for the diversion and re- alignment of drainage should comply with both engineering and environmental requirements in order to provide adequate hydraulic capacity of all drains.	impact from construction site	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	implemented
S5.8.6	Construction works should be programmed to minimize soil excavation works in rainy seasons (April to September). If soil excavation cannot be avoided in these months or at any time of year when rainstorms are likely, for the purpose of preventing soil erosion, temporary exposed slope surfaces should be covered e.g. by tarpaulin, and temporary access	impact from construction site	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	roads should be protected by crushed stone or gravel, as excavation proceeds. Intercepting channels should be provided (e.g. along the crest / edge of excavation) to prevent storm runoff from washing across exposed soil surfaces. Arrangements should always be in place in such a way that adequate surface protection measures can be safely carried out well before the arrival of a rainstorm.						
S5.8.7	Earthworks final surfaces should be well compacted, and the subsequent permanent work or surface protection should be carried out immediately after the final surfaces are formed to prevent erosion caused by rainstorms. Appropriate drainage like intercepting channels should be provided where necessary.	impact from construction site	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	implemented
S5.8.8	Measures should be taken to minimize the ingress of rainwater into trenches. If excavation of trenches in wet seasons is necessary, they should be dug and backfilled in short sections. Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.	impact from construction site	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	implemented
S5.8.9	If bentonite slurries are required for any construction works, they should be reconditioned and reused wherever practicable to minimise the disposal volume of used bentonite slurries. Temporary enclosed storage locations should be provided on-site for any unused bentonite that needs to be transported away after the related construction activities are completed. Requirements as stipulated in ProPECC Note PN 1/94 should be closely followed when handling and disposing bentonite slurries.	impact from construction site	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94	Implemented
\$5.8.10	Open stockpiles of construction materials (e.g. aggregates,	To minimise	Contractor	All works area	Construction	WPCO,	



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	sand and fill material) on sites should be covered with tarpaulin or similar fabric during rainstorms.	impact from construction site run-off			phase	EIAO- TM, ProPECC PN 1/94, TM- DSS	implemented
S5.8.11	Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers. Discharge of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system.	impact from construction site	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	Implemented
S5.8.12	Good site practices should be adopted to remove rubbish and litter from construction sites so as to prevent the rubbish and litter from spreading from the site area. It is recommended to clean the construction sites on a regular basis.	impact from construction site	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	Implemented
\$5.8.12	 The following mitigation measures related to the transportation of the sediment should be implemented to minimize the potential water quality impact: Loading of the excavated sediment to the barge shall be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding water. The barge transporting the sediments to the designated disposal sites shall be equipped with tight fitting seals to prevent leakage and shall not be filled to a level that would cause overflow of materials or laden water during loading or transportation. Monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as 	transportation of sediment	Contractor	Barging point and barges	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94	N/A



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	specified by the Director of Environmental Protection (DEP).						
S5.8.13	There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM- DSS. The beneficial uses of the treated effluent for other on- site activities such as dust suppression, wheel washing and general cleaning etc., can minimise water consumption and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the relevant WPCO licence.	impact from	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	Implemented
S5.8.14	Water for Bored Piling Works Water used in ground boring and drilling for site investigation or rock / soil anchoring should be re-circulated as far as practicable after sedimentation. When there is a need for final disposal, the wastewater should be discharged into storm drains via silt removal facilities.	construction site	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	N/A
S5.8.15	Wheel Washing Water Wash-water from wheel washing facility should have been treated by silt removal facilities before discharging into storm drains. Treated wash-water could be used as dust suppression measures as far as practicable. The section of access road between the wheel washing bay and the public road should be paved to reduce vehicle tracking of soil and to prevent silty water from entering public road and drains.	construction site	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS	implemented



Date

Jun-23

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
\$5.8.16	 Construction Works near Channelized Watercourse / Ditch For minimization of potential water quality impacts from the works to nearby inland channelized watercourse/ditch near SHWSTW, the practices outlined in ProPECC Note PN 1/94 "Construction Site Drainage" and ETWB TC (Works) No.5/2005 "Protection of natural streams / rivers from adverse impacts arising from construction works" should be adopted where applicable. Relevant mitigation measures are listed below: The use of less or smaller construction plants may be specified in works area close to the inland water bodies. Temporary storage of material (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from watercourse/ditch when carrying out of the construction debris and spoil should be covered and located away from any watercourse/ditch. Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the watercourse/ditch, where practicable. Construction effluent, site run-off and sewage should be properly collected and / or treated. 	run-off	Contractor	All works area	Construction phase	WPCO, EIAO- TM, ProPECC PN 1/94, TM- DSS, ETWB TC(Works) No. 5/2005	Implemented
S5.8.17 – S5.8.19	 <u>Accidental Spillage of Chemicals</u> The Contractor should register as a chemical waste producer if chemical wastes would be produced from 		Contractor	All works area	Construction phase	WPCO, EIAO- TM, Waste Disposal	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation, should be observed and complied. Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges. Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows: Suitable containers should be used to hold the chemical waste to avoid leakage or spillage during storage, handling and transport. Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents. Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area. 					Ordinance (WDO), Waste Disposal (Chemical Waste) (General) Regulation	
\$5.8.22 - \$5.8.24	Groundwater from Contaminated Areas, Contaminated Site Runoff and Wastewater from Land Decontamination • Remediation of contaminated land should be properly	To minimise impact from groundwater from	Contractor	All works area confirmed with land	Construction phase	WPCO, EIAO- TM, TM-DSS, Guidance	N/A




EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 conducted following the recommendations of Land Contamination Assessment to be conducted in future. Any excavated contaminated material and exposed contaminated surface should be properly housed and covered to avoid generation of contaminated runoff. Open stockpiling of contaminated materials should not be allowed. Any contaminated runoff or wastewater generated from the land decontamination processes should be properly collected and diverted to wastewater treatment facilities (WTF) as necessary. The WTF shall deploy suitable treatment processes (e.g. oil interceptor/ activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (such as total petroleum hydrocarbon) to an undetectable range. All treated effluent from the wastewater treatment system shall meet the requirements as stated in TM-DSS and should be either discharge of groundwater from contaminated areas should be adopted. Prior to any excavation works within the potentially contaminated areas, the baseline groundwater quality in these areas should be reviewed based on the past relevant site investigation data and any additional groundwater quality measurements to be performed with reference to Guidance Note for Contaminated Land Assessment and Remediation and the review results should be either properly in these areas for the excavation works would be contaminated, this contaminated groundwater should be either properly recharged into the ground in compliance with 	areas, contaminated site run-off/ wastewater from land decontamination		contamination		Note for Contaminate d Land Assessment	



Date

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 the requirements of the TM-DSS. If wastewater treatment is to be deployed for treating the contaminated groundwater, the wastewater treatment unit shall deploy suitable treatment processes (e.g. oil interceptor / activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (such as total petroleum hydrocarbon) to an undetectable range. All treated effluent from the wastewater treatment plant shall meet the requirements as stated in the TM-DSS and should be either discharged into the foul sewers or tankered away for proper disposal. If deployment of wastewater treatment is not feasible for handling the contaminated groundwater, groundwater recharging wells should be installed as appropriate for recharging the contaminated groundwater duality will not be affected by the recharge operation as indicated in section 2.3 of TM-DSS. The baseline groundwater to be recharge wells, and submit a working plan to EPD for agreement. Pollution levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the recharge well. Groundwater monitoring wells should be installed near the recharge wells and to ensure that no likelihood of increase of groundwater level and transfer of pollutants beyond the site boundary. Prior to recharge, free products should be removed as necessary by installing the petrol interceptor. 						



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater recharge operation or discharge of treated groundwater. 						
Waste Man	nagement Implication (Construction Phase)	I	<u> </u>	1	1	1	1
S7.5.3	 Recommendations for good site practices during the construction phase include: Nomination of approved personnel, such as a site manager, to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility; Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste management and chemical waste handling procedures; Provision of sufficient waste reception/ disposal points, and regular collection of waste; Adoption of appropriate measures to minimise windblown litter and dust during transportation of wastes in enclosed containers; Provision of regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; Adoption of a recording system for the amount of wastes generated, recycled and disposed (including the disposal sites); and Preparation of Waste Management Plan (WMP), as part of the Environmental Management Plan (EMP) 	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	Waste Disposal Ordinance (WDO) and Public Cleansing and Prevention of Nuisances Regulation (Cap. 132BK)	Implemented
\$7.5.4	Recommendations to achieve waste reduction are as follow: • Segregate and store different types of construction		Contractor	All works areas	Construction phase	WDO	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	related waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;						
	• Provide separate labelled bins to segregate recyclable waste such as aluminium cans from other general refuse generated by the work force, and to encourage collection by individual collectors;						
	 Recycle any unused chemicals or those with remaining functional capacity; 						
	 Maximise the use of reusable steel formwork to reduce the amount of C&D materials; 						
	 Adopt proper storage and site practices to minimise the potential for damage to, or contamination of construction materials; 						
	 Plan the delivery and stock of construction materials carefully to minimise the amount of waste generated; and 						
	 Minimize over ordering and wastage through careful planning during purchasing of construction materials. 						
S7.5.6	To minimise the impact resulting from collection and transportation of C&D materials as far as practicable, C&D material, such as wood, plastic, steel and other metals should be reused or recycled and, as a last resort, disposed to landfill. A suitable area should be designated within the site for temporary stockpiling of C&D materials and to facilitate the sorting process.	To minimise the disposal of C&D waste	Contractor	All works areas	Construction phase	WDO	Implemented
\$7.5.6	Within the stockpile areas, the following measures should be taken to control potential environmental impacts or nuisance:		Contractor	All works areas	Construction phase	WDO	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 Proper handling and storage of waste such as soil by means of covers and/or water spraying system to minimise the potential environmental impact and to prevent materials from wind-blown or being washed away; 						
	 Covering materials during heavy rainfall; 						
	 Locating stockpiles to minimise potential visual impacts; 						
	 Minimising land intake of stockpile areas as far as possible; 						
	 Adopting GPS or equivalent system for tracking and monitoring of all dump trucks engaged for the Project in recording their travel routings and parking locations to prohibit illegal dumping and landfilling of C&D materials; and 						
	 Keeping record and analysis of data collected by GPS or equivalent system related to travel routings and parking locations of dump trucks engaged on site. 						
S7.5.7 to S7.5.9	General refuse should be stored in enclosed bins or compaction units separate from C&D materials and chemical waste. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D materials and chemical wastes. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light materials.	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	WDO	Implemented
	The recyclable component of general refuse, such as aluminium cans, paper and cleansed plastic containers shall be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste shall be						



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	set up by the Contractor. The Contractor shall also be responsible for arranging recycling companies to collect these materials.						
	The Contractor shall carry out an education programme for workers in avoiding, reducing, reusing and recycling of materials generation. Posters and leaflets advising on the use of the bins shall also be provided in the sites as reminders.						
S7.5.12	If chemical wastes were to be produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer, and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	WDO	Implemented
	Appropriate containers with proper labels should be used for storage of chemical wastes. Chemical wastes should be collected and delivered to designated outlet by a licensed collector. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the CWTC, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.						
	Any unused chemicals or those with remaining functional capacity should be collected for reuse as far as practicable.						
\$7.5.13 to \$7.5.14	The sediment should be excavated, handled, transported and disposed of in a manner that would minimise adverse environmental impacts. For minimization of sediment disposal, beneficial reuse will be considered on site as far as practicable during the construction stage before the disposal	To avoid and minimize impacts arising from waste management	Contractor	All works areas	Construction phase	APCO WDO	N/A



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	of excavated sediment.						
	Requirements of the Air Pollution Ordinance (Construction Dust) Regulation, where relevant, shall be adhered to during excavation, transportation and disposal of sediments.						
S7.5.15	In order to minimise the exposure to contaminated materials, workers shall, when necessary, wear appropriate personal protective equipment (PPE) when handling contaminated sediments. Adequate washing and cleaning facilities shall also be provided on site.	minimize impacts arising from waste	Contractor	All works areas	Construction phase	WDO	N/A
\$7.5.20	Stockpiling of contaminated sediments shall be avoided as far as possible. If temporary stockpiling of contaminated sediments is unavoidable, the excavated sediment shall be covered by tarpaulin and the area shall be placed within earth bunds or sand bags to prevent leachate from entering the ground, nearby drains and/or surrounding water bodies. The stockpiles shall be completely paved or covered by linings in order to avoid contamination to underlying soil or groundwater. Separate and clearly defined areas shall be provided for stockpiling of contaminated and uncontaminated materials. Leachate, if any, shall be collected and discharged according to the Water Pollution Control Ordinance (WPCO).	minimize impacts arising from waste	Contractor	All works areas	Construction phase	WPCO	N/A
S7.5.21	In order to minimise the potential odour / dust emissions during excavation and transportation of the sediment, the excavated sediments shall be wetted during excavation / material handling and shall be properly covered when placed on trucks or barges. Loading of the excavated sediment to the barge shall be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding	minimize impacts arising from waste	Contractor	All works areas	Construction phase	WDO APCO	N/A



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	water.						
Land Cont	amination			1		1	l
\$8.9.3	 To minimise environmental impacts arising from the handling of potentially contaminated materials, the following environmental precautionary measures are recommended to be utilised during the course of any required site remediation: Excavation profiles must be properly designed and executed with attention to the relevant requirements for environment, health and safety; Establish and maintain a Health and Safety Plan with the information below before commencement of the SI: (a) Instruction of works on work procedures, safe practices, emergency duties, and applicable regulations; (b) Regularly scheduled meetings of the workers in which the possible hazards, problems of the job, and related safe practices are emphasized and discussed; (c) Good housekeeping practices; and (d) Availability of and instruction in the location, use and maintenance of personal protective equipment. Excavation shall be carried out during dry season as far as possible to minimise contaminated runoff from contaminated soils; Supply of suitable clean backfill material (or treated soil) after excavation; Stockpiling site(s) shall be lined with impermeable sheeting and bunded. Stockpiles shall be fully covered by impermeable sheeting to reduce dust emission. If this is not practicable due to frequent usage, regular 		Contractor	Area identified with land contamination	Prior to the commencement of construction works at the contaminated areas	"Guidance Note for Contaminated Land Assessment and Remediation" "Guidance Manual for Use of Risk-based Remediation Goals for Contaminated Land Management "Public Cleansing and Prevention of Nuisances Regulation (Cap. 132BK)" APCO, WDO and WPCO	N/A



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
	 watering shall be applied. However, watering shall be avoided on stockpiles of contaminated soil to minimise contaminated runoff; Vehicles containing any excavated materials shall be suitably covered to limit potential dust emissions or contaminated wastewater run-off, and truck bodies and tailgates shall be sealed to prevent any discharge during transport or during wet conditions; Speed control for the trucks carrying contaminated materials shall be enforced; Vehicle wheel and body washing facilities at the site's exist points shall be established and used; and Pollution control measures for air emissions (e.g. from biopile blower and handling of cement), noise emissions (e.g. from blower or earthmoving equipment), and water discharges (e.g. runoff control from treatment facility) shall be implemented and complied with relevant regulations and guidelines. 						
Landscape	and Visual Impact (Construction Phase)						
S9.8.1	Trees unavoidably affected by the works should be transplanted as far as possible in accordance with DEVB TC(W) 7/2015 – Tree Preservation or LAO PN 7/2007 - Tree Preservation and Tree Removal Application for Building Development in Private Projects where applicable.	To transplant affected trees	Contractor	All works areas	Construction phase	DEVB TC(W) No. 7/2015 or LAO PN 7/2007 where applicable	Implemented
S9.8.1	Control of night-time lighting glare.	To minimize the Landscape and visual impact on surrounding setting	Contractor	All works areas	Construction phase	TM-EIAO	Implemented
S9.8.1	Erection of decorative screen hoarding which should be compatible with the surrounding setting.	To minimize the Landscape and visual impact on	Contractor	All works areas	Construction phase	TM-EIAO	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Location of the Measures	Implementation Stage	Requirements	Implementation Status
		surrounding setting					
S9.8.1	Management of facilities on work sites by controlling the height and disposition/arrangement of all facilities on the works site to minimize visual impact to adjacent VSRs.	To minimize visual impact to adjacent VSRs.	Contractor	All works areas	Construction phase	-	Implemented
S9.8.1	All hard and soft landscape areas disturbed temporarily during construction should be reinstated on like-to-like basis, to the satisfaction of the relevant Government Departments.	landscape impact	Contractor	All works areas	Construction phase	-	To be implemented



EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	L-1	
Replanning Works – Contract 1733	Ref#	HKES230400003262	
Monthly EM&A Report		01	
	Date	Jun-23	

APPENDIX L - MONITORING SCHEDULE OF THE REPORTING MONTH



Consultancy Agreement No.NEX/1062 Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works - Advance Constuction Works Dust and Noise Monitoring Schedule in May 2023

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-May	2-May	3-May	4-May	5-May	6-May
				1-hr Dust Monitoring		
7-May	8-May	9-May	10-May	11-May	12-May	13-May
			1-hr Dust Monitoring			
14-May	15-May	16-May	17-May	18-May	19-May	20-May
		1-hr Dust Monitoring				
21-May	22-May	23-May	24-May	25-May	26-May	27-May
	1-hr Dust Monitoring					1-hr Dust Monitoring
28-May	29-May	30-May	31-May			



EP-588/2021 - Siu Ho Wan Station and Siu Ho Wan Depot	Page	M-1	
Replanning Works – Contract 1733	Ref#	HKES230400003262	
Monthly EM&A Report		01	
		Jun-23	

APPENDIX M - MONITORING SCHEDULE OF THE COMING MONTH



Consultancy Agreement No.NEX/1062 Siu Ho Wan Station and Siu Ho Wan Depot Replanning Works - Advance Constuction Works Tentative Dust and Noise Monitoring Schedule in June 2023

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1-Jun	2-Jun	3-Jun
				1-hr Dust Monitoring		
4-Jun	5-Jun	6-Jun	7-Jun	8-Jun	9-Jun	10-Jun
			1-hr Dust Monitoring			
11-Jun	12-Jun	13-Jun	14-Jun	15-Jun	16-Jun	17-Jun
		1-hr Dust Monitoring				
18-Jun	19-Jun	20-Jun	21-Jun	22-Jun	23-Jun	24-Jun
	1-hr Dust Monitoring					1-hr Dust Monitoring
25-Jun	26-Jun	27-Jun	28-Jun	29-Jun	30-Jun	
					1-hr Dust Monitoring	

Remark: The monitoring schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather).
