



**JOB No.: TCS00757/15**

**DSD CONTRACT NO. DC/2013/09 –  
ADVANCE WORKS FOR SHEK WU HUI SEWAGE  
TREATMENT WORKS – FURTHER EXPANSION PHASE 1A  
AND SEWERAGE WORKS AT PING CHE ROAD**

**4<sup>TH</sup> QUARTERLY ENVIRONMENTAL MONITORING AND  
AUDIT (EM&A) SUMMARY REPORT (JULY TO  
SEPTEMBER 2016)**

**PREPARED FOR**

**TSUN YIP WATERWORKS CONSTRUCTION CO LTD**

Date	Reference No.	Prepared By	Certified By
1 November 2016	TCS00757/15/600/R0057v2	 Martin Li (Assistant Environmental Consultant)	 Tam Tak Wing (Environmental Team Leader)

Version	Date	Remarks
1	20 October 2016	First Submission
2	1 November 2016	Amended against IEC's comments



Drainage Services Department  
44/F., Revenue Tower  
5 Gloucester Road  
Wan Chai  
Hong Kong

Your reference:

Our reference: HKDSD201/50/103858

Date: 2 November 2016

Attention: Mr Michael Leung

**BY EMAIL & POST**  
**(email: [hkleung@dsd.gov.hk](mailto:hkleung@dsd.gov.hk))**

Dear Sirs

Agreement No.: SP 01/2015  
Environmental Monitoring and Audit for  
Advance Works for Shek Wu Hui Sewage Treatment Works – Further Expansion Phase 1A  
Quarterly EM&A Report for July to September 2016

We refer to emails of 20 October 2016 and 1 November 2016 attaching a Quarterly EM&A Report for July to September 2016 for the captioned project prepared by the Environmental Team (ET).

We have no further comment and hereby verify the Quarterly EM&A Report.

Please do not hesitate to contact the undersigned at 2618 2836 should you have any queries.

Yours faithfully  
ANewR CONSULTING LIMITED

Adi Lee  
Independent Environmental Checker

LYMA/csym

cc Tsun Yip – Mr Ken Wong (email: [kenwong@tsunyip.hk](mailto:kenwong@tsunyip.hk))  
AUES – Ms Nicola Hon (email: [nicolahon@fordbusiness.com](mailto:nicolahon@fordbusiness.com))

**EXECUTIVE SUMMARY**

ES.01 This is the 4<sup>th</sup> Quarterly Environmental Monitoring and Audit Summary Report for DSD Contract No. DC/2013/09 – Advance Works for Shek Wu Hui Sewage Treatment Works – Further Expansion Phase 1A and Sewerage Works at Ping Che Road (hereinafter referred as “the Contract”) under Environmental Permit number FEP-01/474/2013, covering the period from **1 July to 30 September 2016** (the Reporting Period).

**ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES**

ES.02 Environmental monitoring activities under the EM&A program in this Reporting Period are summarized in the following table.

Issues	Environmental Monitoring Parameters / Inspection	Occasions
Air Quality	1-hour TSP	<b>96</b>
	24-hour TSP	<b>32</b>
Construction Noise	L <sub>Aeq(30min)</sub> Daytime	<b>26</b>
Inspection / Audit	ET Regular Environmental Site Inspection	<b>13</b>
	IEC Monthly Environmental Site Audit	<b>3</b>

**BREACH OF ACTION AND LIMIT (A/L) LEVELS**

ES.03 In the Reporting Period, no exceedance of air quality and construction noise monitoring were recorded. No Notification of Exceedance (NOE) was, therefore, issued. The statistics of environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

Environmental Issues	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Air Quality	1-hour TSP	0	0	0	-	-
	24-hour TSP	0	0	0	-	-
Construction Noise	L <sub>Aeq(30min)</sub>	0	0	0	-	-

Note: NOE – Notification of Exceedance

**SITE INSPECTION**

ES.04 In the Reporting Period, **13** events of joint site inspection to evaluate the site environmental performance by the RE, ET and the Contractor were carried out. No non-compliance was noted.

**ENVIRONMENTAL COMPLAINT**

ES.05 No environmental complaint was recorded or received in this Reporting Period.

**NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS**

ES.06 No environmental summons or successful prosecutions were recorded in this Reporting Period.

**REPORTING CHANGE**

ES.07 No reporting changes were made in the Reporting Period.

**FUTURE KEY ISSUES**

ES.08 As dry season is approaching, special attention should be paid on the potential construction dust impact since most of the construction sites are adjacent to villages. The Contractor should fully implement the construction dust mitigation measures properly.

ES.09 Air quality mitigation measures including wheel wash facilities, watering of haul roads and covering of dusty materials with tarpaulin sheet, etc. should be properly maintained. Moreover, the contractor should be to prevent mosquito breeding on site.

---

**Table of Contents**

<b>1</b>	<b>INTRODUCTION</b>	<b>1</b>
1.1	PROJECT BACKGROUND	1
1.2	REPORT STRUCTURE	2
<b>2</b>	<b>PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS</b>	<b>3</b>
2.1	PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE	3
2.2	CONSTRUCTION PROGRESS	3
2.3	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	4
<b>3</b>	<b>SUMMARY OF IMPACT MONITORING REQUIREMENT</b>	<b>5</b>
3.1	GENERAL	5
3.2	MONITORING PARAMETERS	5
3.3	MONITORING LOCATIONS	5
3.4	MONITORING FREQUENCY AND PERIOD	5
3.5	MONITORING EQUIPMENT	6
3.6	DETERMINATION OF ACTION/LIMIT (A/L) LEVELS	7
3.7	EVENT ACTION PLAN	7
<b>4</b>	<b>MONITORING METHDOLOGY</b>	<b>8</b>
4.1	AIR QUALITY MONITORING	8
4.2	CONSTRUCTION NOISE MONITORING	9
4.3	DATA MANAGEMENT AND DATA QA/QC CONTROL	9
<b>5</b>	<b>IMPACT MONITORING RESULTS</b>	<b>10</b>
5.1	GENERAL	10
5.2	RESULTS OF AIR QUALITY MONITORING	10
5.3	RESULTS OF CONSTRUCTION NOISE MONITORING	10
5.4	CONCLUSION	10
<b>6</b>	<b>WASTE MANAGEMENT</b>	<b>11</b>
6.1	GENERAL WASTE MANAGEMENT	11
6.2	RECORDS OF WASTE QUANTITIES	11
<b>7</b>	<b>SITE INSPECTION</b>	<b>12</b>
7.1	REQUIREMENTS	12
7.2	FINDINGS / DEFICIENCIES DURING THE REPORTING PERIOD	12
<b>8</b>	<b>ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE</b>	<b>14</b>
8.1	ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	14
<b>9</b>	<b>IMPLEMENTATION STATUS OF MITIGATION MEASURES</b>	<b>15</b>
9.1	GENERAL REQUIREMENTS	15
<b>10</b>	<b>CONCLUSIONS AND RECOMMENTATIONS</b>	<b>16</b>
10.1	CONCLUSIONS	16
10.2	RECOMMENDATIONS	16

---

## **LIST OF TABLES**

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	PROPOSED AIR QUALITY AND CONSTRUCTION NOISE MONITORING LOCATIONS
TABLE 3-3	AIR QUALITY MONITORING EQUIPMENT
TABLE 3-4	CONSTRUCTION NOISE MONITORING EQUIPMENT
TABLE 3-5	ACTION AND LIMIT LEVELS FOR 24-HR TSP AND 1-HR TSP AIR QUALITY, $\mu\text{g}/\text{m}^3$
TABLE 3-6	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 5-1	SUMMARY OF AIR QUALITY MONITORING RESULTS
TABLE 5-2	SUMMARY OF NOISE MONITORING RESULTS
TABLE 6-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS FOR THE PROJECT
TABLE 6-2	SUMMARY OF QUANTITIES OF C&D WASTES FOR THE PROJECT
TABLE 7-1	SITE OBSERVATIONS
TABLE 8-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 8-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 8-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 9-1	ENVIRONMENTAL MITIGATION MEASURES

## **LIST OF APPENDICES**

APPENDIX A	GENERAL LAYOUT OF ADVANCE WORKS AND MAIN WORKS OF SWHSTW FURTHER EXPANSION PHASE 1A
APPENDIX B	LAYOUT PLAN OF THE CONTRACT
APPENDIX C	ORGANIZATION STRUCTURE AND CONTACT DETAILS OF RELEVANT PARTIES
APPENDIX D	MASTER CONSTRUCTION PROGRAM OF THE CONTRACT
APPENDIX E	PROPOSED MONITORING LOCATIONS
APPENDIX F	EVENT ACTION PLAN
APPENDIX G	GRAPHICAL PLOTS
APPENDIX H	METEOROLOGICAL INFORMATION
APPENDIX I	MONTHLY SUMMARY WASTE FLOW TABLE
APPENDIX J	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)

## **1 INTRODUCTION**

### **1.1 PROJECT BACKGROUND**

1.1.1 The existing Shek Wu Hui Sewage Treatment Works (hereafter referred as “SWHSTW”) with secondary level treatment to sewage collected from Sheung Shui, Fanling and adjacent areas is operated and maintained by Drainage Services Department (hereafter referred as “DSD”). Based on the preliminary design of the Project, the scope of works for the Project comprises the following major components:

- (a) Demolition of the existing Inlet Works and construction of the new Inlet Works, including inlet pumping station, screening and degritting facilities;
- (b) Demolition of 4 existing circular Primary Sedimentation Tanks (PSTs) and construction of new rectangular PSTs;
- (c) Construction of new pre-membrane screens;
- (d) Modification of existing Bioreactor (BR) 1 and 2 to suit the proposed membrane bioreactor (MBR) process;
- (e) Construction of a new standby Bioreactor;
- (f) Demolition of 4 existing circular Final Sedimentation Tanks (FSTs) and construction of new Membrane Tanks and Membrane Facility Building;
- (g) Reconstruction of sludge treatment facilities, including thickening, anaerobic digestion, biogas handling, sludge holding and dewatering facilities; and
- (h) Other ancillary works.

1.1.2 According to the Project implementation programme, the construction of most of the above proposed works (hereinafter referred to as “Main Works”) will be commencement in 2016 and completion in 2022. Furthermore, Advance Works as part of the above proposed works will carry out before Main Works commencement. The Advance Works will be commencement in third quarter of 2015 and comprise the following major components:

- (a) Modification of BR1, through upgrading of electrical and mechanical (E&M) equipment and minor civil works, to suit the proposed MBR process;
- (b) Demolition of FSTs 1 and 2 and construction of Membrane Tanks and the first phase of Membrane Facility Building; and
- (c) Tree felling and transplanting, to facilitate timely construction of the new Inlet Works during the implementation of Main Works (under review).

1.1.3 The general layout of Advance Works and Main Works of SWHSTW Further Expansion Phase 1A show in **Appendix A**. Subsequent to Further Expansion Phase 1A, the SWHSTW will be further expanded under separate projects (namely Further Expansion Phase 1B and Phase 2).

1.1.4 In July 2015, Tsun Yip Waterworks Construction Co Ltd (hereinafter referred as “Tsun Yip” or “the Contractor”) has awarded the DSD Contract No. DC/2013/09 – **Advance Works for Shek Wu Hui Sewage Treatment Works – Further Expansion Phase 1A and Sewerage Works at Ping Che Road** (hereinafter referred as “the Contract”). The Contract is the Advance Works for Shek Wu Hui Sewage Treatment Works as part of SWHSTW Further Expansion which is a Designated Project under Environmental Permit number FEP-01/474/2013 (hereinafter referred as “the FEP-01/474/2013” or “the EP”).

1.1.5 The works under the Contract at Shek Wu Hui Sewage Treatment Works will be included the conversion of one existing bioreactor and two existing final sedimentation tanks into one membrane bioreactor. Moreover, construction of about 1.5 kilometres length of sewers at Ping Che Road and other ancillary works will be undertaken. The works of Contract are scheduled to be conduct about 25 months. Layout plan of the Contract is shown in **Appendix B**.

1.1.6 Action-United Environmental Services & Consulting (hereinafter referred as “AUES”) was



appointed by the Contractor as an Environmental Team (hereinafter referred as “the ET”) to implement the relevant EM&A program in accordance with the Updated EM&A Manual, as well as the associated duties.

- 1.1.7 As part of the EM&A program, baseline monitoring is required to determine the ambient environmental conditions. Hence baseline monitoring including air quality and noise were carried out between **28 August 2015** and **12 September 2015** at the proposed locations before construction work commencement. The “Baseline Monitoring Report (TCS00757/15/600/R0014 Version 2)” had submitted to EPD by the DSD before commencement of major construction works and verified by the IEC on 30 September 2015. Further to Tsun Yip’s instructions, the EM&A program was commenced on 1 October 2015 and the monitoring schedule had been issued to relevant parties on 29 September 2015.
- 1.1.8 This is the **4<sup>th</sup>** Quarterly EM&A Report for the Project presenting the monitoring results and inspection findings for the reporting period from **1 July to 30 September 2016**.

## **1.2 REPORT STRUCTURE**

- 1.2.1 The Quarterly Environmental Monitoring and Audit (EM&A) Summary Report is structured into the following sections:-

<b>SECTION 1</b>	<b>INTRODUCTION</b>
<b>SECTION 2</b>	<b>PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS</b>
<b>SECTION 3</b>	<b>SUMMARY OF MONITORING REQUIREMENTS</b>
<b>SECTION 4</b>	<b>IMPACT MONITORING RESULTS</b>
<b>SECTION 5</b>	<b>WASTE MANAGEMENT</b>
<b>SECTION 6</b>	<b>SITE INSPECTIONS</b>
<b>SECTION 7</b>	<b>ENVIRONMENTAL COMPLAINTS AND NON-COMPLIANCE</b>
<b>SECTION 8</b>	<b>IMPLEMENTATION STATUES OF MITIGATION MEASURES</b>
<b>SECTION 9</b>	<b>IMPACT FORECAST</b>
<b>SECTION 10</b>	<b>CONCLUSIONS AND RECOMMENDATION</b>

## **2 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS**

### **2.1 PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE**

- 2.1.1 Organization structure and contact details of relevant parties with respect to on-site environmental management are shown in [Appendix C](#).

### **2.2 CONSTRUCTION PROGRESS**

- 2.1.2 Master Construction Program of the Contract is enclosed in [Appendix D](#) and the major construction activities undertaken in this Reporting Period are illustrated in [Appendix B](#) and listed below:-

#### **July 2016**

- Excavation to formation level +0.3mPD (At Membrane Facilities Building)
- Concreting the blinding layer (At Membrane Facilities Building)
- Welding the ELS (At Membrane Facilities Building)
- Excavation to formation level +2.4mPD (At Membrane Tank)
- Backfilling the DN900 open trench (Near Final Sedimentation Tank No.5)
- Laying the remaining DN1400 pipe (Near Common Channel of BR2)
- Backfilling and removal sheet pile for DN1400 open trench (Near Common Channel of BR2)
- Rebar fixing, formwork erection and concreting the wall opening at BR2 (Near Common Channel of BR2)
- Rebar fixing, formwork erection and concreting the wall opening at MH Type J (Near Common Channel of BR1)
- Open Excavation, backfilling and pipe laying for Cable Duct (Near Bioreactor No.3)
- Concrete Breaking for Carriageway (Near Control Room No.2)

#### **August 2016**

- Welding for Pile Head Steel Plate (At Membrane Facilities Building)
- Erection of Formwork and Falsework (At Membrane Facilities Building)
- Preparation of Re-bar Fixing Works (At Membrane Facilities Building)
- Excavation and Installation of Sheet Pile for DN900 Trench (Near Final Sedimentation Tank No.5)
- Restore BR2 and Suspend BR1 (At BR1 and BR2 Common Channel)
- Deposition and Compaction of Coarse Aggregate on Carriageway (V.O.6, Near Control Room No.2)
- Concreting the 100mm THK Wall on Carriageway (V.O.6, Near Control Room No.2)

#### **September 2016**

- Concreting the pile cap and base slab (At Membrane Facilities Building)
- Erection and dismantle formwork (At Membrane Facilities Building)
- Installation of sheet pile, open excavation and installation of DN900 (Near Final Sedimentation Tank No.5)
- Installation of steel plate to block the sewage flow (At common liquor channel)
- Laying HBCA No.5 and Construction of Field Equipment Pit#1 & Pedestrian Trial Panel (V.O.6 Porous Pavement)



## 2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.1.3 Summary of the relevant permits, licences, and/or notifications on environmental protection for this Project in this Reporting Period is presented in [Table 2-1](#).

**Table 2-1 Status of Environmental Licenses and Permits**

Item	Description	License/Permit Status
1	Air Pollution Control (Construction Dust) Regulation	Notified EPD on 30 July 2015
2	Chemical waste Producer Registration (WPN: 5213-624-T3148-04)	Application date: 19/08/2015 Date approved: 18/9/2015
3	Water Pollution Control Ordinance (Discharge License: WT00022503-2015)	Application date: 19/08/2015 Date approved: 18/9/2015
4	Billing Account for Disposal of Construction Waste (Account Number: 7022898)	Granted on 02/09/2015

2.1.4 In accordance with the Further EP No. FEP-01/474/2013 Condition 2.3, an Updated Environmental Monitoring and Audit (EM&A) Manual (TCS00757/15/600/R0012v3) which certified by the Environmental Team (ET) Leader and verified by the Independent Environmental Checker (IEC), has submitted to DSD and EPD endorsement.

2.1.5 Baseline Monitoring Report (TCS00757/15/600/R0014v2) as certified by the ETL and verified by the IEC was submitted to the EPD on 30 September 2015 for endorsement.

**3 SUMMARY OF IMPACT MONITORING REQUIREMENT****3.1 GENERAL**

3.1.1 The Environmental Monitoring and Audit requirements are set out in the Updated EM&A manual. Environmental issues such as air quality and construction noise were identified as the key issues during the construction phase of Advance Works of the Project. A summary of EM&A programme of construction phase are presented in the sub-sections below.

**3.2 MONITORING PARAMETERS**

3.2.1 The EM&A programmes of construction phase shall cover the following environmental issues:

- Air quality; and
- Construction noise

3.2.2 A summary of the monitoring parameters is presented in *Table 3-1* below

**Table 3-1 Summary of EM&A Requirements**

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> <li>• 1-hour TSP by Real-Time Portable Dust Meter; and</li> <li>• 24-hour TSP by High Volume Air Sampler.</li> </ul>
Construction Noise	<ul style="list-style-type: none"> <li>• <math>L_{eq(30min)}</math> during normal working hours; and</li> <li>• <math>L_{eq(15min)}</math> for the construction works undertaken in Restricted Hours, if necessary.</li> </ul>

**3.3 MONITORING LOCATIONS**

3.3.1 According to the *Updated EM&A Manual* of Advance Works which submitted to EPD on **25 August 2015**, three air quality sensitive receivers and two construction noise sensitive receivers are proposed to monitor the environmental performance of the Contract. The proposed monitoring locations are summarized in *Table 3-2* and shown in *Appendix E*.

**Table 3-2 Proposed Air Quality and Construction Noise Monitoring Locations**

Aspect	Station ID	Location	Parameter
Air Quality	AM1	No. 31 Wai Loi Tsuen	1- hour and 24- hour TSP
	AM2	Fu Tei Au	1- hour
	AM2a	RE's Site Office	24- hour TSP
Noise	NM1	No. 31 Wai Loi Tsuen	$L_{eq(30min)}$
	NM2	Fu Tei Au	$L_{eq(30min)}$

**3.4 MONITORING FREQUENCY AND PERIOD**

3.4.1 The requirements of baseline monitoring are stipulated in *Sections 2.1.7 and 3.2.5* of the Updated *EM&A Manual* and presented as follows.

*Air Quality Monitoring*

3.4.2 Monitoring frequency for air quality baseline monitoring is as follows:

- 1-Hour TSP      3 sets of 1-hour TSP monitoring shall be carried out once in every six days.
- 24-Hour TSP      24-hour shall be carried out once in every six days.

*Noise Monitoring*

3.4.3 Construction noise monitoring should be carried out at the designated monitoring station when there are Project-related construction activities being undertaken within a radius of 300m from the monitoring stations. The monitoring frequency should depend on the scale of the

construction activities. An initial guide on the monitoring is to obtain one set of 30-minute measurement at each station between 0700 and 1900 hours on normal weekdays at a frequency of once a week when construction activities are underway.

- 3.4.4 If construction works are extended to include works during the hours of 1900 - 0700, additional weekly impact monitoring shall be carried out during evening and night-time works. Applicable permits under NCO shall be obtained by the Contractor.

### 3.5 MONITORING EQUIPMENT

#### Air Quality Monitoring

- 3.5.1 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If the ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to the IEC to approve.
- 3.5.2 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.
- 3.5.3 All equipment as used air quality monitoring is listed in **Table 3-3**.

**Table 3-3 Air Quality Monitoring Equipment**

Equipment	Model
<b>24-Hr TSP</b>	
High Volume Air Sampler	TISCH High Volume Air Sampler, HVS Model TE-5170
Calibration Kit	TISCH Model TE-5025A
<b>1-Hour TSP</b>	
Portable Dust Meter	Sibata LD-3 Laser Dust monitor Particle Mass Profiler & Counter

#### Wind Data Monitoring Equipment

- 3.5.4 According to the Updated EM&A Manual Sections 2.1.3.8, alternative methods to obtain representative wind data was proposed by the ET. Meteorological information as extracted from “the Hong Kong Observatory Ta Kwu Ling Station” is alternative method to obtain representative wind data. For Ta Kwu Ling Station, it is located nearby the Project site. Moreover, this station is situated the sea level above 15mPD. The station’s wind data monitoring equipment is set above the existing ground ten meters in compliance with the general setting up requirement. Furthermore, this station also can be to provide the humidity, rainfall, and air pressure and temperature etc. meteorological information. In Hong Kong of a lot development projects, weather information extracted from Hong Kong Observatory is common alternative method if weather station installation not allowed.

#### Noise Monitoring

- 3.5.5 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m s<sup>-1</sup>.
- 3.5.6 Noise monitoring equipment to be used for baseline monitoring is listed in **Table 3-4**.

**Table 3-4 Construction Noise Monitoring Equipment**

Equipment	Model
Integrating Sound Level Meter	Rion NL-52 or Rion NL-31 or BK2238
Calibrator	Rion NC-73 / CB-5 / BK4231

Equipment	Model
Portable Wind Speed Indicator	Testo Anemometer

- 3.5.7 Sound level meters listed above comply with the *International Electrotechnical Commission Publications 651: 1979 (Type 1)* and *804: 1985 (Type 1)* specifications, as recommended in TM issued under the NCO. The acoustic calibrator and sound level meter to be used in the baseline monitoring will be calibrated yearly.

### 3.6 DETERMINATION OF ACTION/LIMIT (A/L) LEVELS

- 3.6.1 According to the baseline monitoring results and the Updating Environmental Monitoring and Audit Manual stipulation, the air quality and construction noise criteria were set up, namely Action and Limit levels are listed in *Tables 3-5 & 3-6* as below.

**Table 3-5 Action and Limit Levels for 24-Hr TSP and 1-Hr TSP Air Quality,  $\mu\text{g m}^{-3}$**

Monitoring Stations	Action Level ( $\mu\text{g/m}^3$ )		Limit Level ( $\mu\text{g/m}^3$ )	
	1-hour	24-hour	1-hour	24-hour
AM1	286	147	500	260
AM2	276	NA	500	NA
AM2a	NA	155	NA	260

**Table 3-6 Action and Limit Levels for Construction Noise**

Monitoring Stations	Action Level	Limit Level in dB(A)
Time Period: 0700-1900 hours on normal weekdays		
NM1 and NM2	When one documented complaint is received	> 75* dB(A)

Note: (\*) Reduces to 70 dB(A) for schools and 65 dB(A) during the school examination periods.

### 3.7 EVENT ACTION PLAN

- 3.7.1 If non-compliance or exceedance of the Action/Limit Levels is occurred, actions shall be taken in accordance with the Event Action Plan in *Appendix F*.

## **4 MONITORING METHDOLOGY**

### **4.1 AIR QUALITY MONITORING**

#### **Monitoring Location**

- 4.1.1 The detailed information of air quality monitoring stations referred to *Table 3-2* and the graphical plot of monitoring locations shown in *Appendix E* in this report.

#### **Monitoring Equipment**

- 4.1.2 All the monitoring equipment to be used in the EM&A program as listed in *Table 3-3* has been agreed with the IEC.

#### **Monitoring Procedures**

##### 1-hour TSP

- 4.1.3 The 1-hour TSP monitor, a Sibata LD-3 Laser Dust monitor Particle Mass Profiler & Counter was used for baseline monitoring, which is a portable, battery-operated laser photometer. The 1-hour TSP meter provides a real time 1-hour TSP measurement based on 90<sup>0</sup> light scattering. The 1-hour TSP monitor consisted of the following:

- a. A pump to draw sample aerosol through the optic chamber where TSP is measured;
- b. A sheath air system to isolate the aerosol in the chamber to keep the optics clean for maximum reliability; and
- c. A built-in data logger compatible with Windows based program to facilitate data collection, analysis and reporting.

- 4.1.4 The 1-hour TSP meter used is within the valid period, calibrated by the manufacturer prior to purchasing. Zero response of the instrument was checked before and after each monitoring event. Operation of the 1-hour TSP meter was follow manufacturer's Operation and Service Manual. A valid calibration certificate is attached in *Appendix G*.

##### 24-hour TSP

- 4.1.5 The equipment used for 24-hour TSP measurement is a Tisch Environmental, Inc. Model TE-5170 TSP high volume air sampling system, which complied with EPA Code of Federal Regulation, Appendix B to Part 50. The High Volume Air Sampler (HVS) consists of the following:

- a. An anodized aluminum shelter;
- b. A 8"x10" stainless steel filter holder;
- c. A blower motor assembly;
- d. A continuous flow/pressure recorder;
- e. A motor speed-voltage control/elapsed time indicator;
- f. A 7-day mechanical timer, and
- g. A power supply of 220v/50 hz

- 4.1.6 Prior of 24-hour TSP monitoring, the HVS was calibrated in accordance with the manufacturer's instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5028A). The 24-hour TSP Monitoring using the HVS was also processed in accordance with the manufacturer's Operations Manual. A valid calibration certificate of the calibration kit with the certificate of HVS calibrated is attached in *Appendix G*.

- 4.1.7 24-hour TSP was collected by the ET on filters of HVS and quantified by a local HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd (ALS), upon receipt of the samples. The ET keeps all the sampled 24-hour TSP filters in normal air conditioned room conditions, i.e. 70% HR (Relative Humidity) and 25°C, for six months prior to disposal.

## **4.2 CONSTRUCTION NOISE MONITORING**

### **Monitoring Location**

- 4.2.1 The detailed information of construction noise monitoring stations referred to **Table 3-2** and the graphical plot of monitoring locations shown in **Appendix E** in this report.

### **Monitoring Equipment**

- 4.2.2 All the monitoring equipment to be used in the EM&A program as listed in **Table 3-3** has been agreed with the IEC.
- 4.2.3 Sound level meter listed in **Table 3-4** is complied with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications, as recommended in Technical Memorandum (TM) issued under the Noise Control Ordinance (NCO). A valid of calibration certificates including sound level meter and an acoustic were shown in **Appendix G**.

### **Monitoring Procedures**

- 4.2.4 The noise measurement was performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq). Leq(30min) in six consecutive Leq(5 min) measurements were used as the monitoring parameter throughout the baseline monitoring period.
- 4.2.5 During the monitoring, the sound level meter was mounted on a tripod at a height of about 1.2 m and placed at the monitoring locations and oriented such that the microphone was pointed to the site with the microphone facing perpendicular to the line of sight. The windshield was fitted for the measurement. For construction noise monitoring, all monitoring stations were conducted 1 m from the exterior of the building façade.
- 4.2.6 Prior noise measurement, the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. The calibration level from before and after the noise measurement agrees to within 1.0dB.
- 4.2.7 During the noise measurement, a portable wind speed meter was used to check wind speed (m/s). For baseline noise monitoring, no wind speed was exceeding 5m/s or gusts exceeding 10m/s. Also, noise measurement in time was no fog and rain.

## **4.3 DATA MANAGEMENT AND DATA QA/QC CONTROL**

- 4.3.1 The monitoring data were handled by the ET's in-house data recording and management system.
- 4.3.2 The monitoring data recorded in the equipment were downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data were input into a computerized database properly maintained by the ET. The laboratory results were input directly into the computerized database and checked by personnel other than those who input the data.
- 4.3.3 For monitoring parameters that require laboratory analysis, the local laboratory shall follow the QA/QC requirements as set out under the HOKLAS scheme for the relevant laboratory tests.



**5 IMPACT MONITORING RESULTS****5.1 GENERAL**

- 5.1.1 Since the major construction work of the Project commenced on 1 October 2015, air quality and noise monitoring at the designated locations were therefore performed.

**5.2 RESULTS OF AIR QUALITY MONITORING**

- 5.2.1 In the Reporting Period, a total of **96** events of 1-hour TSP and **32** events of 24-hour TSP monitoring were performed. The summary of air quality monitoring in the Reporting Period is shown in **Tables 5-1** and the relevant graphical plots are shown in **Appendix G**.

**Table 5-1 Summary of Air Quality Monitoring Results**

Monitoring Location	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )			24-hour TSP ( $\mu\text{g}/\text{m}^3$ )		
	Min	Max	Average	Min	Max	Average
AM1	30	161	54	19	126	50
Record Date	20-Jul-16	8-Jul-16	48 events	18-Jul-16	30-Sep-16	16 events
AM2/ AM2a	34	181	62	11	93	34
Record Date	20-Jul-16	8-Jul-16	48 events	2-Sep-16	12-Jul-16	16 events

- 5.2.2 In the Reporting Period, the 24-hour and 1-hour TSP monitoring results were below the Action/ Limit Level. No Notification of Exceedances (NOE) of air quality criteria or corrective action was therefore required.

**5.3 RESULTS OF CONSTRUCTION NOISE MONITORING**

- 5.3.1 In the Reporting Period, a total of **26** event noise measurements were carried out at the designated locations. During construction noise monitoring, the sound level meter was set in 1m from the exterior of the building façade. Therefore, no façade correction (+3dB(A)) is added according to acoustical principles and EPD guidelines. The construction noise monitoring results at the designated locations are summarized in **Table 5-2** and the relevant graphical plots are shown in **Appendix G**.

**Table 5-2 Summary of Construction Noise Monitoring Results**

Monitoring Location	Leq, 30min (dB(A))	
	Min	Max
NM1	52	60
Record Date	1-Aug-16	5-Sep-16
NM2	49	56
Record Date	20-Jul-16, 18-Aug-16, 24-Aug-16, 15-Sep-16, 21-Sep-16	5-Sep-16

- 5.3.2 As shown in **Table 5-2**, the noise level measured at the designated monitoring locations were below 75dB(A). Furthermore, there was no noise complaints (Action Level exceedance) received by the RE, Contractors or DSD in the Reporting Period. Therefore, no Action or Limit Level exceedance was triggered and no corrective action was required.

**5.4 CONCLUSION**

- 5.4.1 In view of the monitoring result throughout the Reporting Period, there were no exceedances recorded in respect to air quality and noise monitoring. It indicated that the implemented mitigation measures are effectively to minimize the impact attributable to the construction works. Moreover, the set of data collected under monitoring work are with statistical power to categorically identify or confirm the absence of impact attributable to the works.

**6 WASTE MANAGEMENT****6.1 GENERAL WASTE MANAGEMENT**

- 6.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

**6.2 RECORDS OF WASTE QUANTITIES**

- 6.2.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

- 6.2.2 The quantities of waste for disposal in this Reporting Period are summarized in **Tables 6-1** and **6-2** and the Summary Waste Flow Table is shown in **Appendix I**. Whenever possible, materials were reused on-site as far as practicable.

**Table 6-1 Summary of Quantities of Inert C&D Materials for the Project**

Type of Waste	Quantity					Disposal Location
	Previous months	Jul 16	Aug 16	Sep 16	Cumulated	
C&D Materials (Inert) (in '000m <sup>3</sup> )	8.317	3.284	0.396	0.529	12.526	--
Hard Rock and Large Broken Concrete (Inert) (in '000m <sup>3</sup> )	1.284	0	0.005	0	1.289	Tuen Mun 38
Reused in this Project (Inert) (in '000 m <sup>3</sup> )	0.522	0.150	0.100	0.100	0.872	--
Reused in other Projects (Inert) (in '000 m <sup>3</sup> )	2.228	0	0	0	2.228	--
Disposal as Public Fill (Inert) (in '000 m <sup>3</sup> )	4.283	3.134	0.291	0.429	8.137	Tuen Mun 38

**Table 6-2 Summary of Quantities of C&D Wastes for the Project**

Type of Waste	Quantity					Disposal Location
	Previous months	Jul 16	Aug 16	Sep 16	Cumulated	
Metals ('000kg)	113.51	0	4.720	0	118.23	Licensed collector
Paper / Cardboard Packing ('000kg)	0	0	0	0	0	--
Plastics ('000kg)	0	0	0	0	0	--
Chemical Wastes ('000kg)	0	0	0	0	0	--
General Refuses ('000m <sup>3</sup> )	0.127	0.002	0.012	0.008	0.149	NENT

**7 SITE INSPECTION****7.1 REQUIREMENTS**

- 7.1.1 According to the Updated EM&A Manual, the environmental site inspection shall be formulated by ET Leader. Weekly environmental site inspections should carry out to confirm the environmental performance.

**7.2 FINDINGS / DEFICIENCIES DURING THE REPORTING PERIOD**

- 7.2.1 In the Reporting Period, joint site inspection to evaluate the site environmental performance by the RE, ET and the Contractor has been carried out on **6, 12, 19 and 26 July 2016, 4, 9, 16, 23 and 30 August 2016, 6, 12, 19 and 27 September 2016**. Furthermore, IEC attend site inspection was on **26 July 2016, 30 August 2016 and 27 September 2016**. No non-compliance was noted.
- 7.2.2 Observations for the site inspections and audit within this Reporting Period are summarized in **Table 7-1**.

**Table 7-1 Site Observations**

<b>Date</b>	<b>Findings / Deficiencies</b>	<b>Follow-Up Status</b>
6 July 2016	<ul style="list-style-type: none"> <li>No adverse environmental issue was observed during site inspection.</li> </ul>	<ul style="list-style-type: none"> <li>Nil.</li> </ul>
12 July 2016	<ul style="list-style-type: none"> <li>The Contractor was reminded to clean the sludge on the paved work area.</li> </ul>	<ul style="list-style-type: none"> <li>Not required for reminder.</li> </ul>
19 July 2016	<ul style="list-style-type: none"> <li>Accumulation of construction waste was observed. The contractor was advised to dispose construction waste regularly.</li> <li>Chemical containers were reminded to spray water on unpaved haul road regularly.</li> </ul>	<ul style="list-style-type: none"> <li>Construction waste was disposed. Last observation closed.</li> <li>Not required for reminder.</li> </ul>
26 July 2016	<ul style="list-style-type: none"> <li>The Contractor was reminded to provide water spraying regularly on site to reduce dust generation.</li> </ul>	<ul style="list-style-type: none"> <li>Not required for reminder.</li> </ul>
4 August 2016	<ul style="list-style-type: none"> <li>No adverse environmental issue was observed during site inspection.</li> </ul>	<ul style="list-style-type: none"> <li>Nil.</li> </ul>
9 August 2016	<ul style="list-style-type: none"> <li>Oil stain was observed on the ground. The contractor was advised to clean the oil stain and dispose as chemical waste.</li> <li>The contractor was reminded to spray water on unpaved haul road regularly.</li> </ul>	<ul style="list-style-type: none"> <li>Oil stain was removed.</li> <li>Not required for reminder.</li> </ul>
16 August 2016	<ul style="list-style-type: none"> <li>Sludge were observed on the ground. The contractor was advised to clear the sludge.</li> <li>The contractor was advised to spray mosquito oil on stagnant water.</li> </ul>	<ul style="list-style-type: none"> <li>Sludge was removed from the ground.</li> <li>Mosquito oil was sprayed on the stagnant water</li> </ul>
23 August 2016	<ul style="list-style-type: none"> <li>The Contractor was reminded to carry out water spraying regularly on site to reduce dust generation.</li> </ul>	<ul style="list-style-type: none"> <li>Not required for reminder.</li> </ul>
30 August 2016	<ul style="list-style-type: none"> <li>Crane idling without engine turned off was observed. The Contractor should turn off the idling vehicle to reduce air impact on site.</li> <li>The Contractor was reminded to remove the spilled chemical and treat as chemical waste at MFB to avoid land contamination.</li> </ul>	<ul style="list-style-type: none"> <li>No idling vehicle was observed on-site.</li> <li>Not required for reminder.</li> </ul>
6 September	<ul style="list-style-type: none"> <li>The contractor was reminded to clean the</li> </ul>	<ul style="list-style-type: none"> <li>Not required for</li> </ul>

<b>Date</b>	<b>Findings / Deficiencies</b>	<b>Follow-Up Status</b>
2016	stagnant water on-site after raining.	reminder.
12 September 2016	<ul style="list-style-type: none"><li>• Accumulation of general waste was observed. The contractor was advised to dispose it regularly.</li><li>• The Contractor was cover stockpiles with tarpaulin sheet.</li></ul>	<ul style="list-style-type: none"><li>• General waste was disposed.</li><li>• Not required for reminder.</li></ul>
19 September 2016	<ul style="list-style-type: none"><li>• The Contractor was reminded to spray water at unpaved dry work area.</li></ul>	<ul style="list-style-type: none"><li>• Not required for reminder.</li></ul>
27 September 2016	<ul style="list-style-type: none"><li>• The Contractor was reminded to provide sufficient disposal facilities for general refuse on site.</li></ul>	<ul style="list-style-type: none"><li>• Not required for reminder.</li></ul>

**8 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE****8.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION**

- 8.1.1 No environmental complaint, summons and prosecution was received in this reporting period. The statistical summary table of environmental complaint, environmental summons and environmental prosecution are presented in [Tables 8-1, 8-2 and 8-3](#).

**Table 8-1 Statistical Summary of Environmental Complaints**

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
1 – 31 July 2016	0	0	NA
1 – 31 August 2016	0	0	NA
1 – 30 September 2016	0	0	NA

**Table 8-2 Statistical Summary of Environmental Summons**

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Complaint Nature
1 – 31 July 2016	0	0	NA
1 – 31 August 2016	0	0	NA
1 – 30 September 2016	0	0	NA

**Table 8-3 Statistical Summary of Environmental Prosecution**

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Complaint Nature
1 – 31 July 2016	0	0	NA
1 – 31 August 2016	0	0	NA
1 – 30 September 2016	0	0	NA

## 9 IMPLEMENTATION STATUS OF MITIGATION MEASURES

### 9.1 GENERAL REQUIREMENTS

- 9.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the Updated EM&A Manual covered the issues of dust, noise, water and waste and they are summarized presented in **Appendix J**.
- 9.1.2 The Contract under the Project shall be implementing the required environmental mitigation measures according to the Updated EM&A Manual as subject to the site condition. Environmental mitigation measures generally implemented by the Contract in this Reporting Period are summarized in **Table 9-1**.

**Table 9-1 Environmental Mitigation Measures**

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> <li>Wastewater to be treated by the filtration systems i.e. sedimentation tank before to discharge.</li> </ul>
Air Quality	<ul style="list-style-type: none"> <li>Maintain wet surface on access road</li> <li>All vehicles must use wheel washing facility before off site</li> <li>Sprayed water during breaking works</li> <li>A cleaning truck was regularly performed on the public road to prevent fugitive dust emission</li> </ul>
Noise	<ul style="list-style-type: none"> <li>Restrain operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday.</li> <li>Keep good maintenance of plants</li> <li>Shut down the plants when not in used.</li> </ul>
Waste and Chemical Management	<ul style="list-style-type: none"> <li>On-site sorting prior to disposal</li> <li>Follow requirements and procedures of the “Trip-ticket System”</li> <li>Predict required quantity of concrete accurately</li> <li>Collect the unused fresh concrete at designated locations in the sites for subsequent disposal</li> </ul>
General	<ul style="list-style-type: none"> <li>The site was generally kept tidy and clean.</li> </ul>

- 9.1.3 Based on monitoring results including air quality and construction noise, it is considered that the environmental mitigation measures implemented by the Contractor in this Reporting Period are effective.



---

**10 CONCLUSIONS AND RECOMMENTATIONS**

**10.1 CONCLUSIONS**


- 10.1.1 This is the 4<sup>th</sup> Quarterly EM&A Report for the Project presenting the monitoring results and inspection findings for the reporting period from **1 July 2016 to 30 September 2016**.
- 10.1.2 No 24-hour or 1-hour TSP monitoring results that triggered the Action or Limit Levels were recorded. No NOEs or the associated corrective actions were therefore issued.
- 10.1.3 No noise complaint (which is an Action Level exceedance) was received and no construction noise measurement results that exceeded the Limit Level were recorded in this Reporting Period. No NOEs or the associated corrective actions were therefore issued.
- 10.1.4 No documented complaint, notification of summons or successful prosecution was received.
- 10.1.5 In the Reporting Period, **13** events of joint site inspection to evaluate the site environmental performance by the RE, ET and the Contractor were carried out. No non-compliance was noted.
- 10.1.6 No site inspection was undertaken by any external party in this Reporting Period.


**10.2 RECOMMENDATIONS**

- 10.2.1 As dry season is approaching, special attention should be paid on the potential construction dust impact since most of the construction sites are adjacent to villages. The Contractor should fully implement the construction dust mitigation measures properly.
- 10.2.2 Air quality mitigation measures including wheel wash facilities, watering of haul roads and covering of dusty materials with tarpaulin sheet, etc. should be properly maintained.
- 10.2.3 To control the site performance on waste management, Tsun Yip shall ensure that all solid and liquid waste management works are fully in compliance with the relevant license/permit requirements, such as the effluent discharge licence and the chemical waste producer registration. Tsun Yip is also reminded to implement the recommended environmental mitigation measures according to the Updated Environmental Monitoring and Audit Manual.

## **Appendix A**

### **GENERAL LAYOUT OF ADVANCE WORKS AND MAIN WORKS OF SWHSTW FURTHER EXPANSION PHASE 1A**

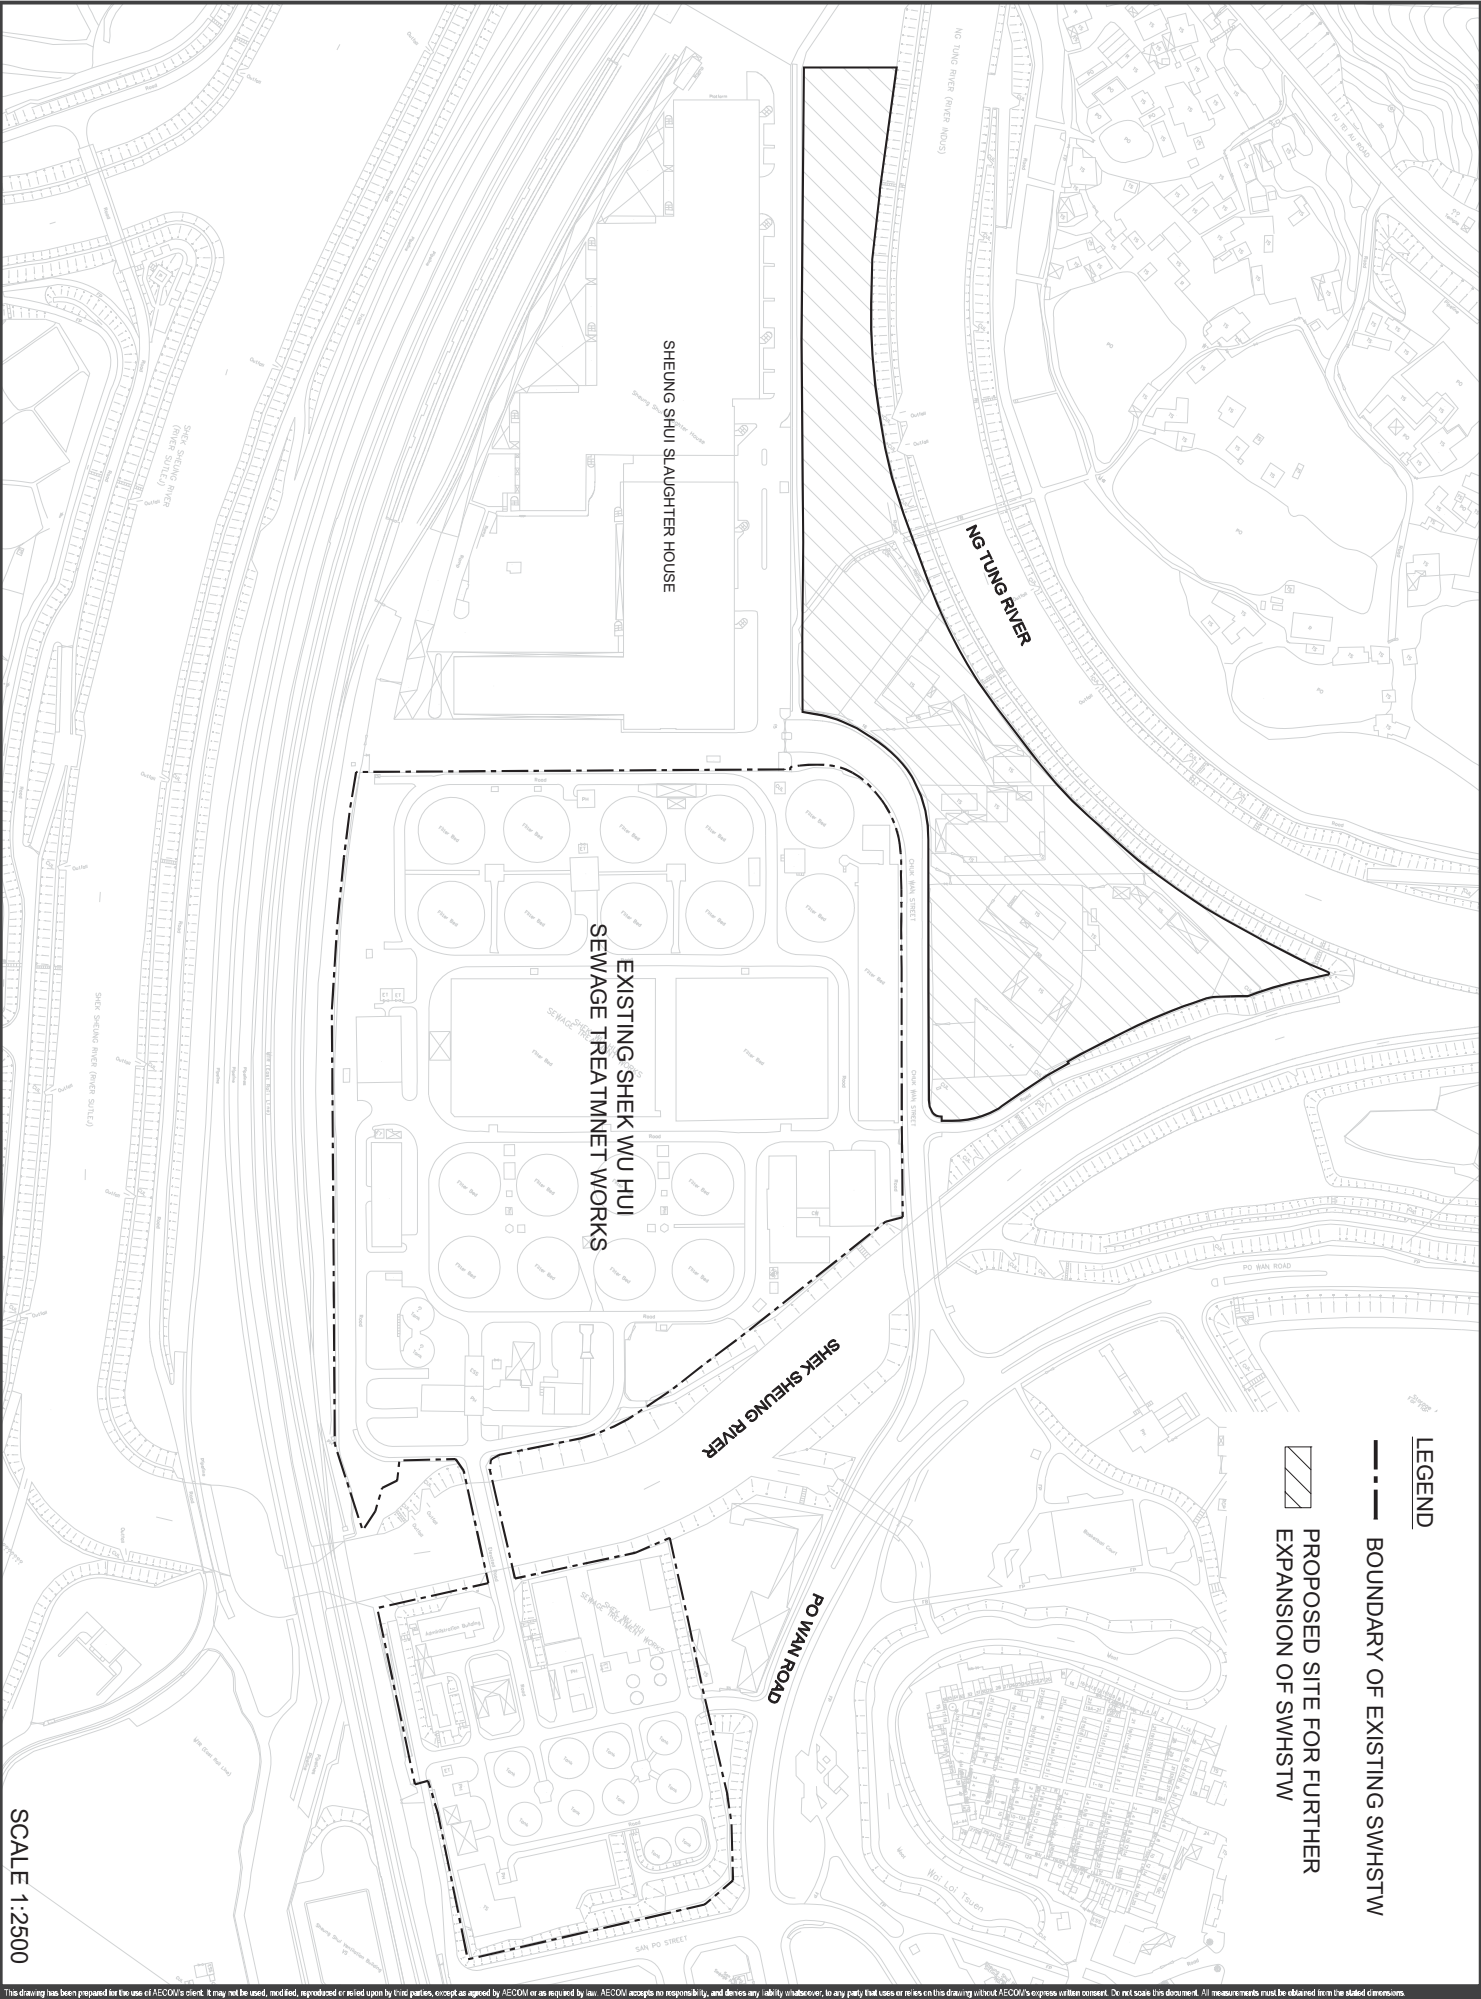

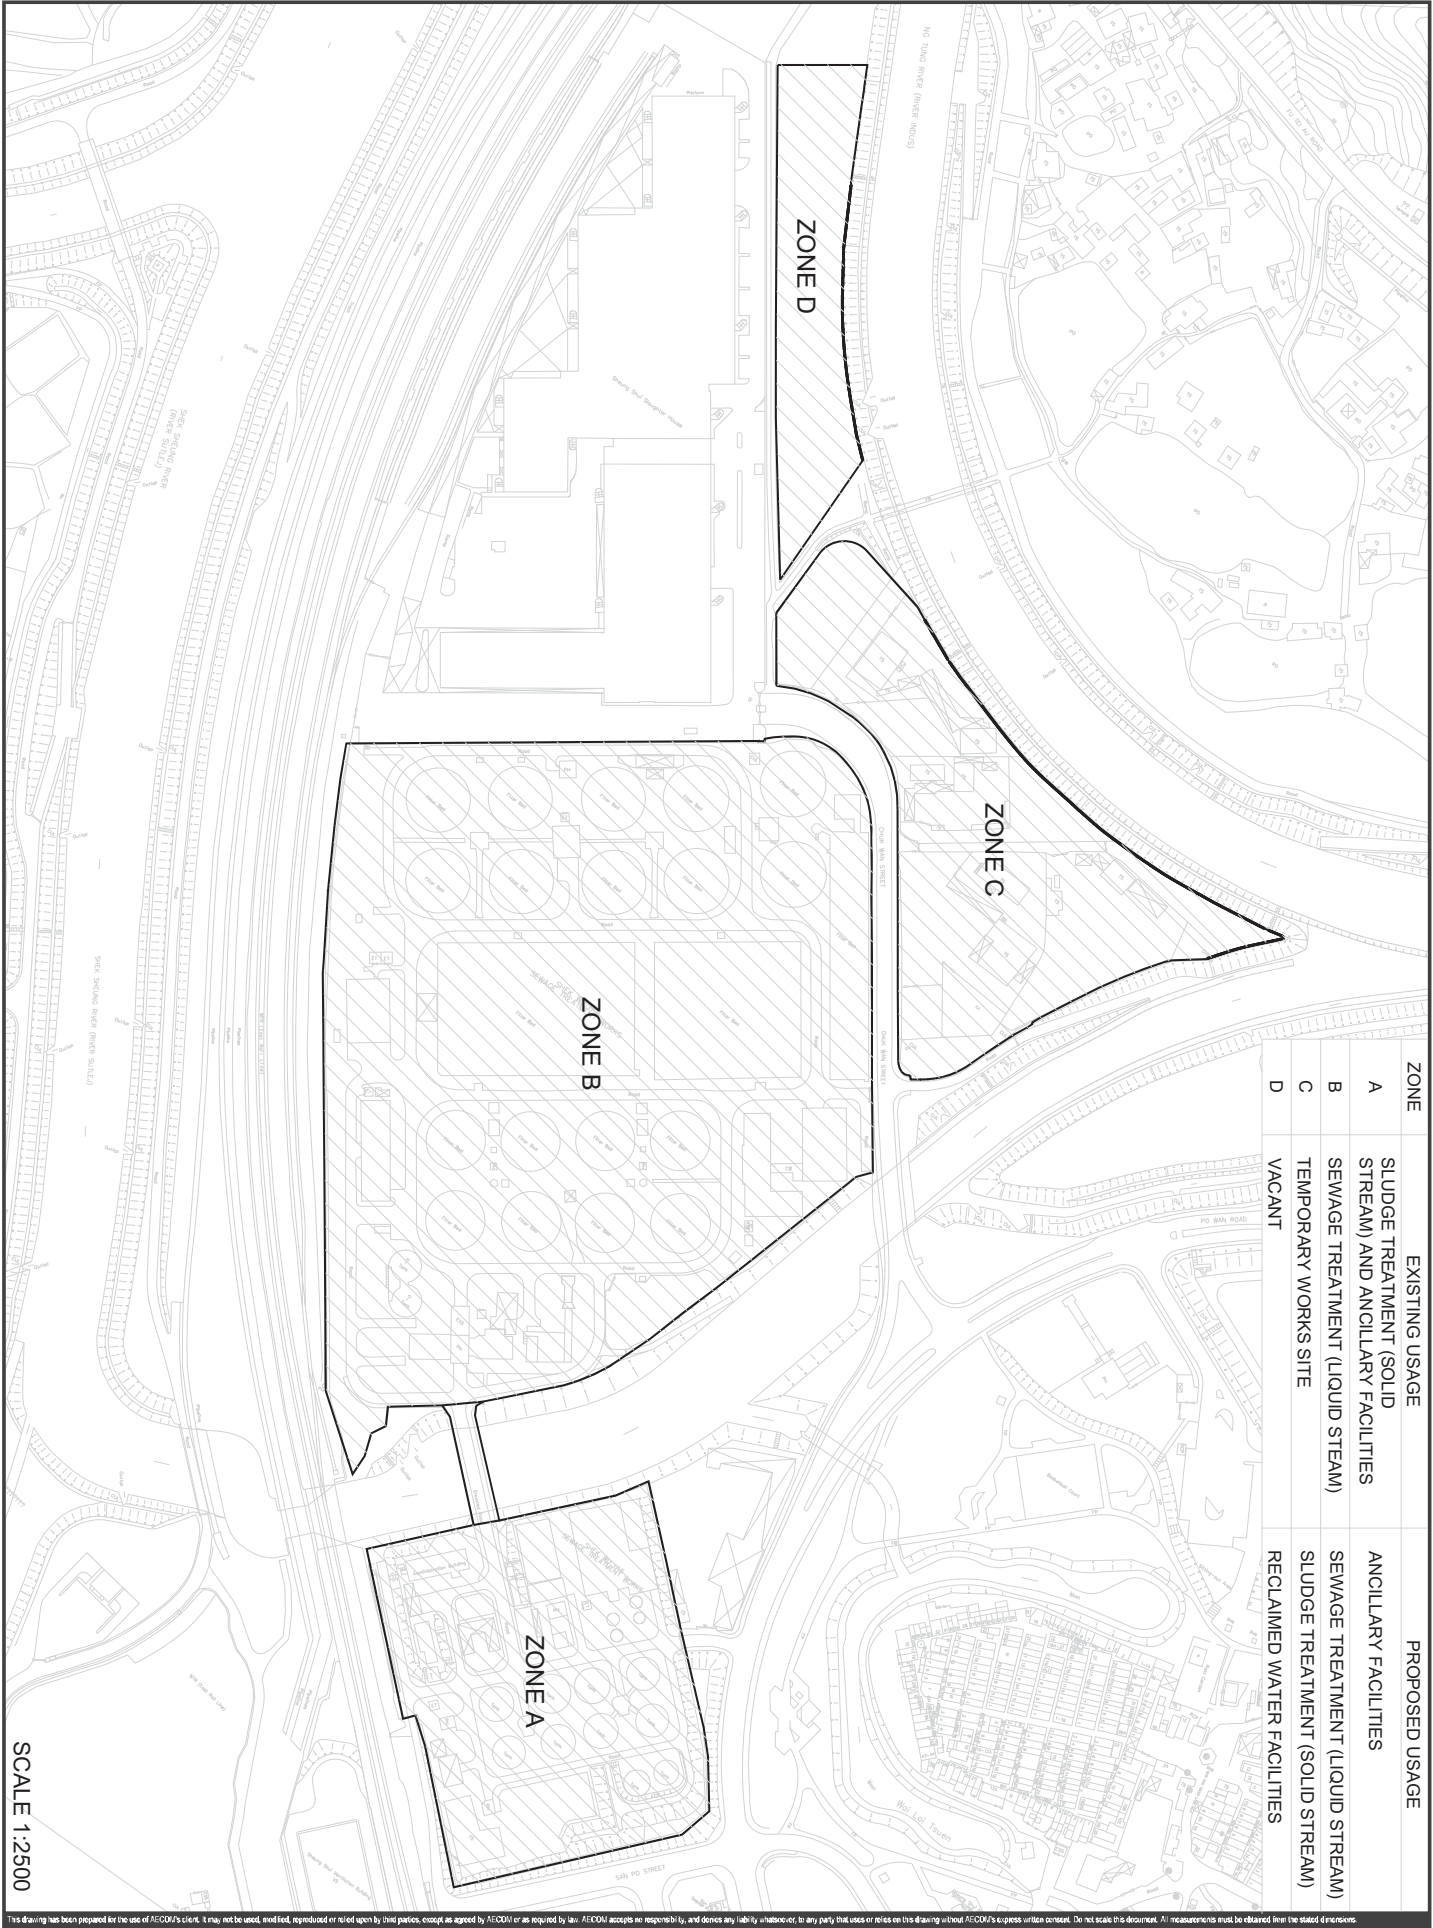


SCALE 1:2500

## **Appendix B**

### **LAYOUT PLAN OF ADVANCE WORKS**



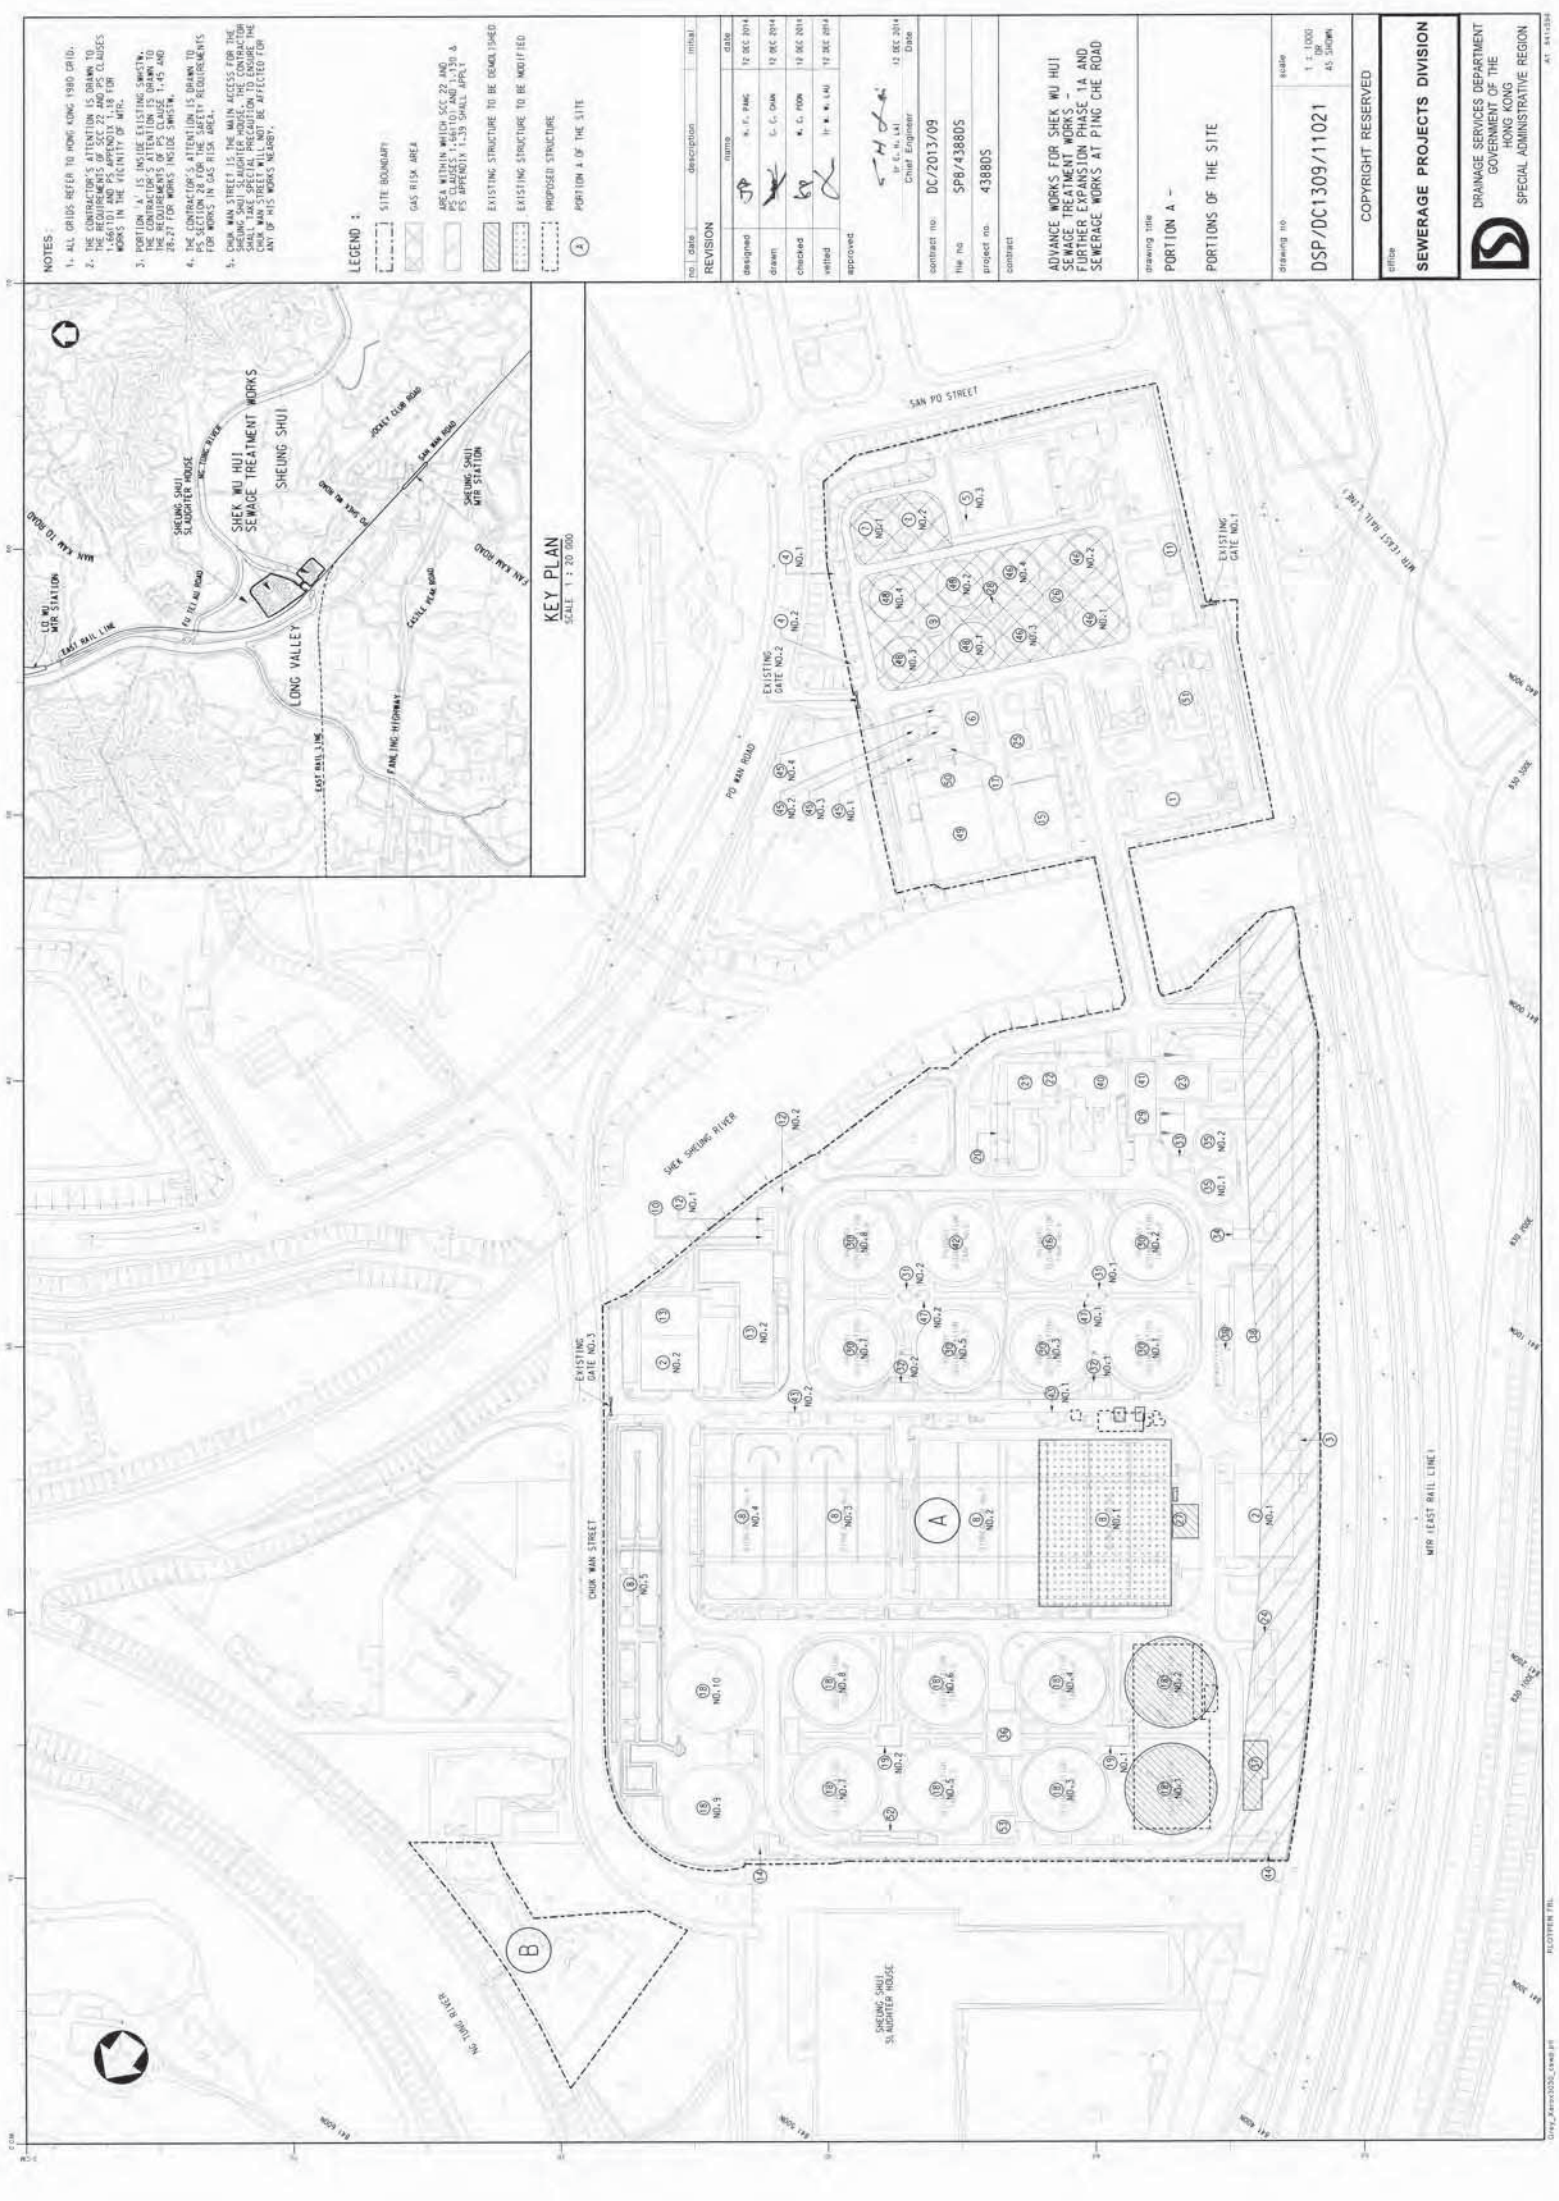

**NOTES:**

1. ALL GRIDS REFER TO HONG KONG 1980 GRID.
2. THE CONTRACTOR'S ATTENTION IS DRAWN TO THE FOLLOWING: (a) THE WORKS ARE TO BE CONSTRUCTED IN ACCORDANCE WITH THE SPECIFICATIONS AND PS APPENDIX 1, 2, 3 AND 4 FOR WORKS IN THE VICINITY OF MTR.
3. PORTION 'A' IS INSIDE EXISTING SWGTW. THE CONTRACTOR'S ATTENTION IS DRAWN TO THE FOLLOWING: (a) THE WORKS ARE TO BE CONSTRUCTED IN ACCORDANCE WITH THE SPECIFICATIONS AND PS APPENDIX 1, 2, 3 AND 4 FOR WORKS IN THE VICINITY OF MTR.
4. THE CONTRACTOR'S ATTENTION IS DRAWN TO THE FOLLOWING: (a) THE WORKS ARE TO BE CONSTRUCTED IN ACCORDANCE WITH THE SPECIFICATIONS AND PS APPENDIX 1, 2, 3 AND 4 FOR WORKS IN THE VICINITY OF MTR.
5. CHOW WAN STREET IS THE MAIN ACCESS FOR THE WORKS. THE CONTRACTOR'S ATTENTION IS DRAWN TO THE FOLLOWING: (a) THE WORKS ARE TO BE CONSTRUCTED IN ACCORDANCE WITH THE SPECIFICATIONS AND PS APPENDIX 1, 2, 3 AND 4 FOR WORKS IN THE VICINITY OF MTR.

- LEGEND:**
- SITE BOUNDARY
  - GAS RISER AREA
  - AREA WITHIN WHICH SCC 22 AND PS CLAUSES 1, 4, 10, 11 AND 11.33, 11.35, 11.36, 11.37, 11.38, 11.39, 11.40 AND 11.41 APPLY
  - EXISTING STRUCTURE TO BE DEMOLISHED
  - EXISTING STRUCTURE TO BE MODIFIED
  - PROPOSED STRUCTURE
  - PORTION A OF THE SITE

REV.	DATE	DESCRIPTION	INITIAL
<b>REVISION</b>			
1	12 DEC 2014	DESIGN	
2	12 DEC 2014	DESIGN	
3	12 DEC 2014	DESIGN	
4	12 DEC 2014	DESIGN	
5	12 DEC 2014	DESIGN	
6	12 DEC 2014	DESIGN	
7	12 DEC 2014	DESIGN	
8	12 DEC 2014	DESIGN	
9	12 DEC 2014	DESIGN	
10	12 DEC 2014	DESIGN	
11	12 DEC 2014	DESIGN	
12	12 DEC 2014	DESIGN	
13	12 DEC 2014	DESIGN	
14	12 DEC 2014	DESIGN	
15	12 DEC 2014	DESIGN	
16	12 DEC 2014	DESIGN	
17	12 DEC 2014	DESIGN	
18	12 DEC 2014	DESIGN	
19	12 DEC 2014	DESIGN	
20	12 DEC 2014	DESIGN	
21	12 DEC 2014	DESIGN	
22	12 DEC 2014	DESIGN	
23	12 DEC 2014	DESIGN	
24	12 DEC 2014	DESIGN	
25	12 DEC 2014	DESIGN	
26	12 DEC 2014	DESIGN	
27	12 DEC 2014	DESIGN	
28	12 DEC 2014	DESIGN	
29	12 DEC 2014	DESIGN	
30	12 DEC 2014	DESIGN	
31	12 DEC 2014	DESIGN	
32	12 DEC 2014	DESIGN	
33	12 DEC 2014	DESIGN	
34	12 DEC 2014	DESIGN	
35	12 DEC 2014	DESIGN	
36	12 DEC 2014	DESIGN	
37	12 DEC 2014	DESIGN	
38	12 DEC 2014	DESIGN	
39	12 DEC 2014	DESIGN	
40	12 DEC 2014	DESIGN	
41	12 DEC 2014	DESIGN	
42	12 DEC 2014	DESIGN	
43	12 DEC 2014	DESIGN	
44	12 DEC 2014	DESIGN	
45	12 DEC 2014	DESIGN	
46	12 DEC 2014	DESIGN	
47	12 DEC 2014	DESIGN	
48	12 DEC 2014	DESIGN	
49	12 DEC 2014	DESIGN	
50	12 DEC 2014	DESIGN	
51	12 DEC 2014	DESIGN	
52	12 DEC 2014	DESIGN	
53	12 DEC 2014	DESIGN	
54	12 DEC 2014	DESIGN	
55	12 DEC 2014	DESIGN	
56	12 DEC 2014	DESIGN	
57	12 DEC 2014	DESIGN	
58	12 DEC 2014	DESIGN	
59	12 DEC 2014	DESIGN	
60	12 DEC 2014	DESIGN	
61	12 DEC 2014	DESIGN	
62	12 DEC 2014	DESIGN	
63	12 DEC 2014	DESIGN	
64	12 DEC 2014	DESIGN	
65	12 DEC 2014	DESIGN	
66	12 DEC 2014	DESIGN	
67	12 DEC 2014	DESIGN	
68	12 DEC 2014	DESIGN	
69	12 DEC 2014	DESIGN	
70	12 DEC 2014	DESIGN	
71	12 DEC 2014	DESIGN	
72	12 DEC 2014	DESIGN	
73	12 DEC 2014	DESIGN	
74	12 DEC 2014	DESIGN	
75	12 DEC 2014	DESIGN	
76	12 DEC 2014	DESIGN	
77	12 DEC 2014	DESIGN	
78	12 DEC 2014	DESIGN	
79	12 DEC 2014	DESIGN	
80	12 DEC 2014	DESIGN	
81	12 DEC 2014	DESIGN	
82	12 DEC 2014	DESIGN	
83	12 DEC 2014	DESIGN	
84	12 DEC 2014	DESIGN	
85	12 DEC 2014	DESIGN	
86	12 DEC 2014	DESIGN	
87	12 DEC 2014	DESIGN	
88	12 DEC 2014	DESIGN	
89	12 DEC 2014	DESIGN	
90	12 DEC 2014	DESIGN	
91	12 DEC 2014	DESIGN	
92	12 DEC 2014	DESIGN	
93	12 DEC 2014	DESIGN	
94	12 DEC 2014	DESIGN	
95	12 DEC 2014	DESIGN	
96	12 DEC 2014	DESIGN	
97	12 DEC 2014	DESIGN	
98	12 DEC 2014	DESIGN	
99	12 DEC 2014	DESIGN	
100	12 DEC 2014	DESIGN	

**ADVANCE WORKS FOR SHEK WU HUI SEWAGE TREATMENT WORKS 1A AND SEWERAGE WORKS AT PING CHE ROAD**

drawing title  
**PORTION A -**  
**PORTIONS OF THE SITE**

drawing no.  
**DSP/DC1309/11021**


copyright reserved

**SEWERAGE PROJECTS DIVISION**  
DRAINAGE SERVICES DEPARTMENT  
GOVERNMENT OF THE  
HONG KONG  
SPECIAL ADMINISTRATIVE REGION

AT 141034

AT 141034



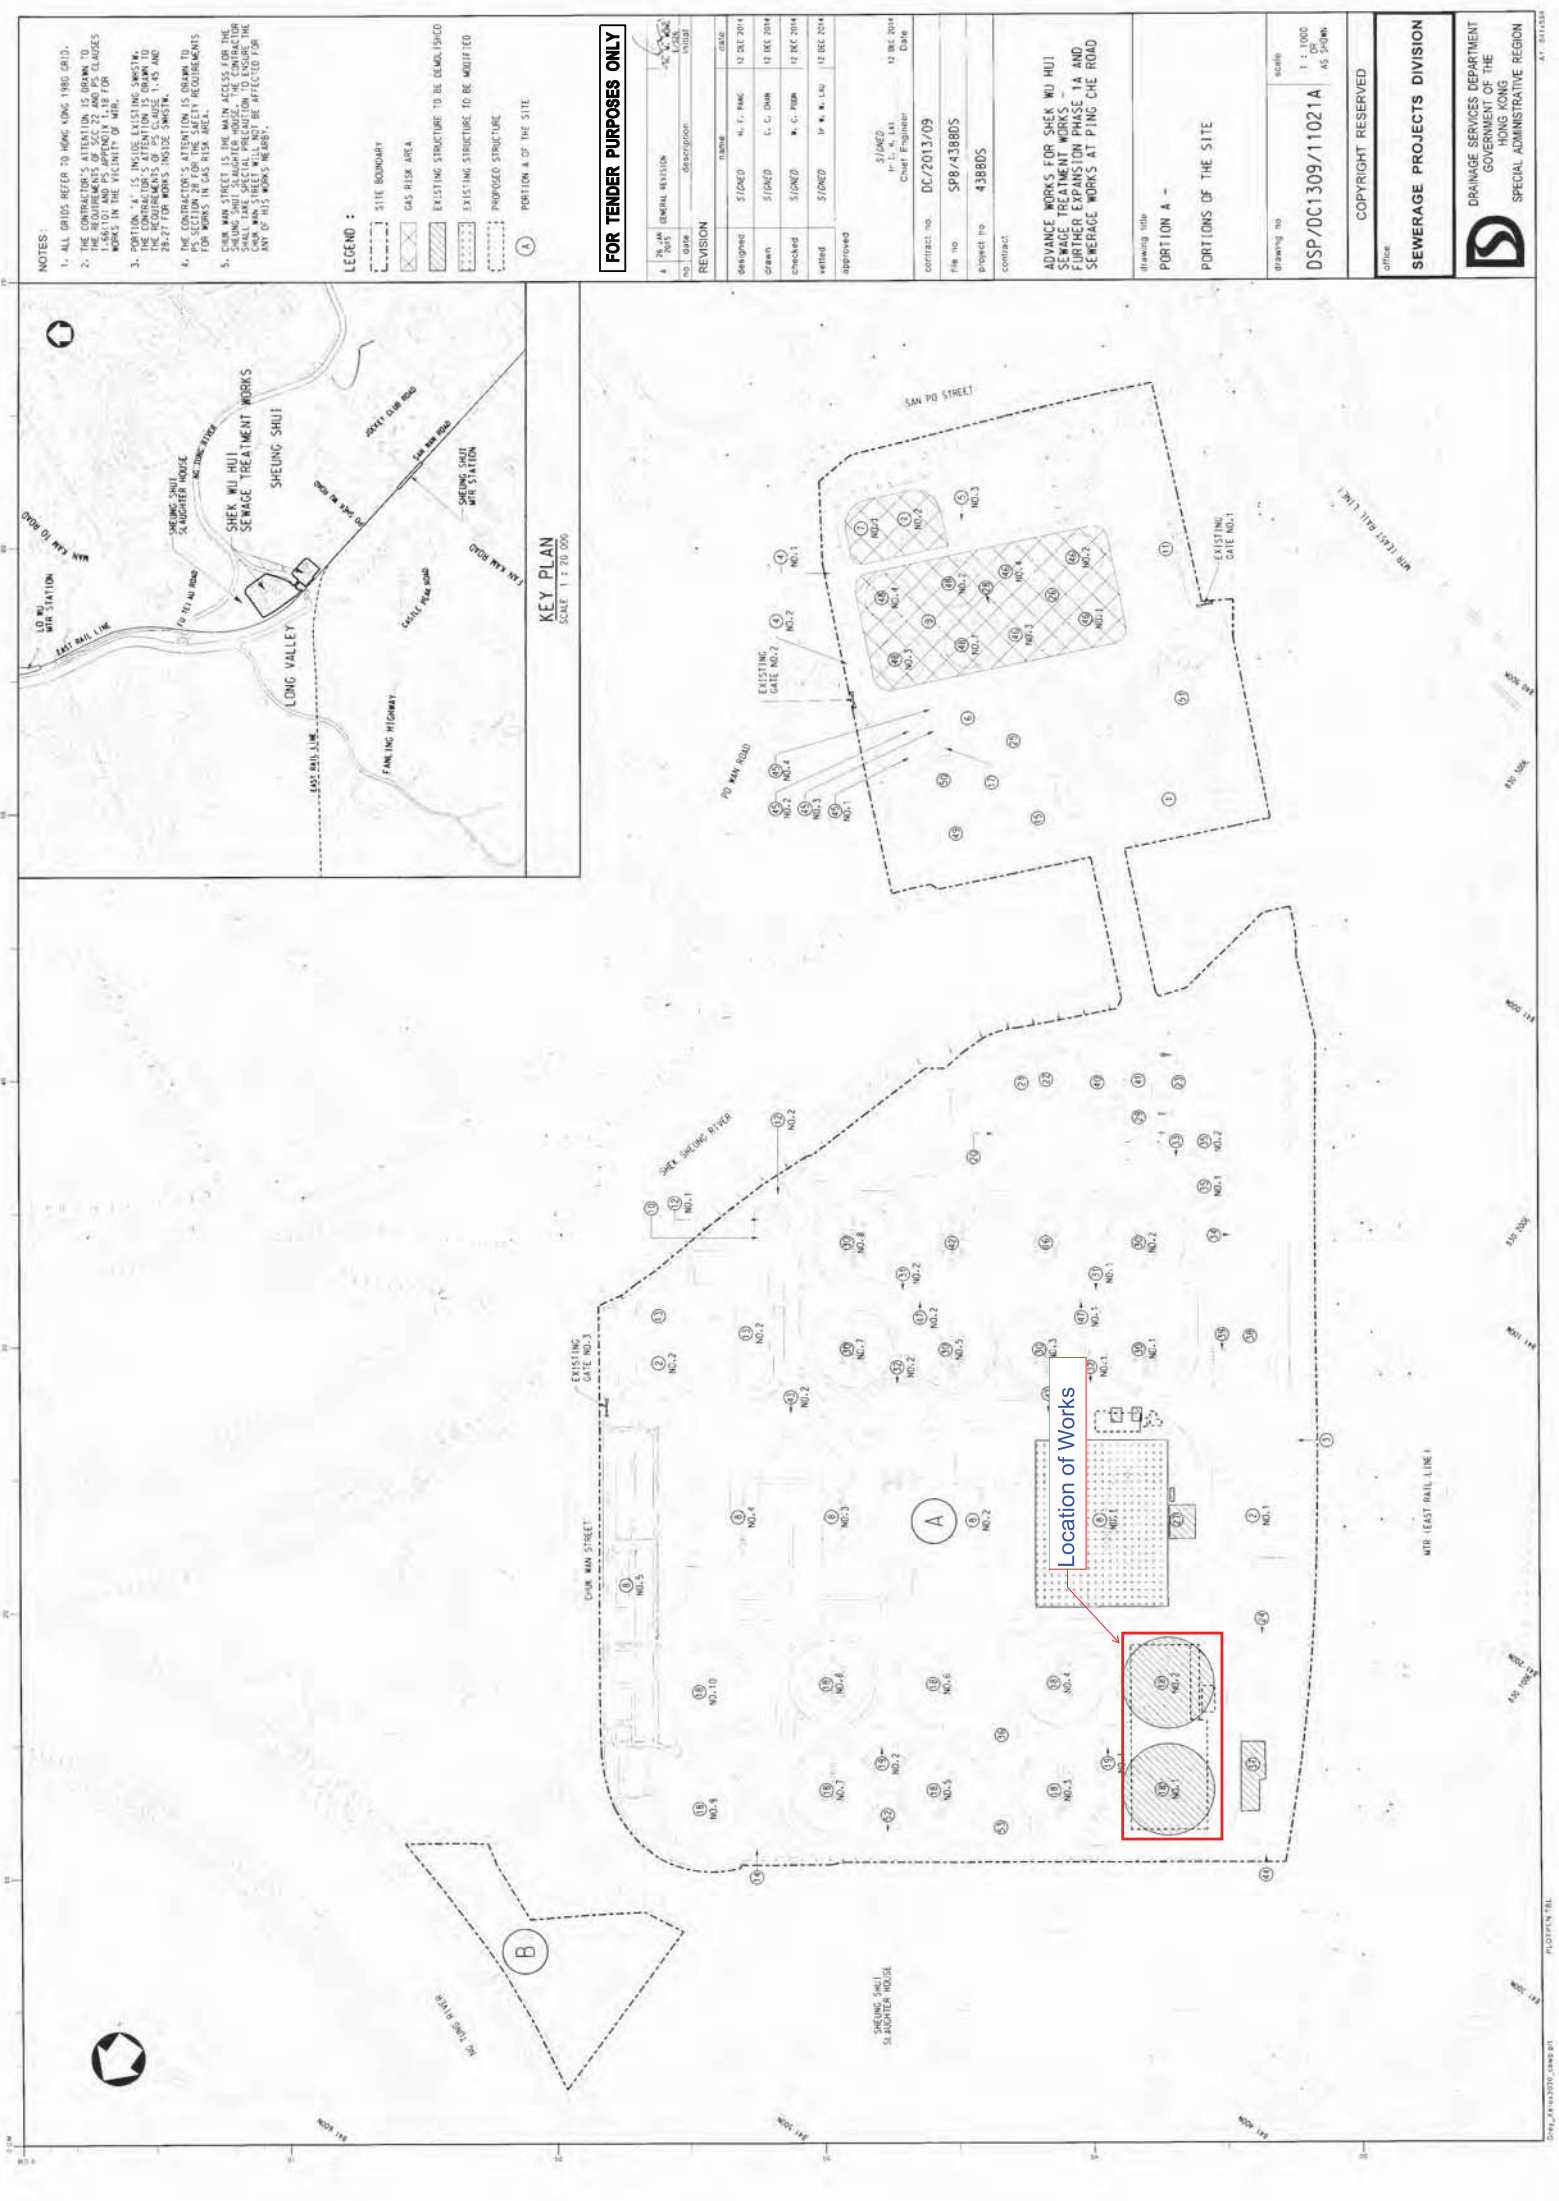

- NOTES:**
1. ALL GRIDS REFER TO HONG KONG 1980 GRID.
  2. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE RELEVANT AUTHORITIES.
  3. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE RELEVANT AUTHORITIES.
  4. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE RELEVANT AUTHORITIES.
  5. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE RELEVANT AUTHORITIES.
- LEGEND:**
- 1. SITE BOUNDARY
  - 2. GAS RISK AREA
  - 3. EXISTING STRUCTURE TO BE DEMOLISHED
  - 4. EXISTING STRUCTURE TO BE MODIFIED
  - 5. PROPOSED STRUCTURE
  - 6. PORTION A OF THE SITE

FOR TENDER PURPOSES ONLY	
GENERAL REVISION	
NO.	DESCRIPTION
1	DESIGNED
2	DRAWN
3	CHECKED
4	VERIFIED
5	APPROVED
DATE	
DESIGNED	12 DEC 2014
DRAWN	12 DEC 2014
CHECKED	12 DEC 2014
VERIFIED	12 DEC 2014
APPROVED	12 DEC 2014
ST/DCD	12 DEC 2014
Chief Engineer	
Contract no.	DC/2013/09
File no.	SPB/438805
Project no.	438805
Contract	
ADVANCE WORKS FOR SHEK WU HUI SEWAGE TREATMENT WORKS - FURTHER EXPANSION PHASE 1A AND SEWERAGE WORKS AT PING CHE ROAD	
PORTION A - PORTIONS OF THE SITE	
Drawing title	
Scale	1 : 1000
Drawing no.	DSP/DC/1309/11021A
COPYRIGHT RESERVED	
SEWERAGE PROJECTS DIVISION	
DRAINAGE SERVICES DEPARTMENT GOVERNMENT OF THE HONG KONG SPECIAL ADMINISTRATIVE REGION	

## **Appendix C**

### **ORGANIZATION STRUCTURE AND CONTACT DETAILS OF RELEVANT PARTIES**

**Contact Details of Relevant Parties**

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
DSD	Resident Site Engineer	Mr. Michael Leung	2594 7463	2827 8700
ANewR	Independent Environmental Checker	Mr. Adi Lee	2618 2836	3007 8648
Tsun Yip	Project Director	Mr. K. C. KAN	2633 4181	2633 4691
Tsun Yip	Project Manager	Mr. M. T. HO	9507 9634	2633 4691
Tsun Yip	Site Agent	Mr. Ken WONG	9161 9627	2633 4691
Tsun Yip	Environmental Officer	Ms. FONG Ka Ying	6312 1871	2633 4691
AUES	Environmental Team Leader	Mr. T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Mr. Ben Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Mr. Martin Li	2959 6059	2959 6079

**Legend:**

*DSD (Employer & Resident Site Engineer) – Drainage Service Department*

*Tsun Yip (Main Contractor) – Tsun Yip Waterworks Construction Co Ltd*


*ANewR (IEC) – ANewR Consulting Limited*

*AUES (ET) – Action-United Environmental Services & Consulting*

## **Appendix D**

### **MASTER CONSTRUCTION PROGRAM**

**Contract DC/2013/09**  
Advance Works for Shek Wu Hui Sewage Treatment Works -  
Further Expansion Phase 1A and Sewage Works at Ping Che Road  
**Works Programme (Sep 2015)**

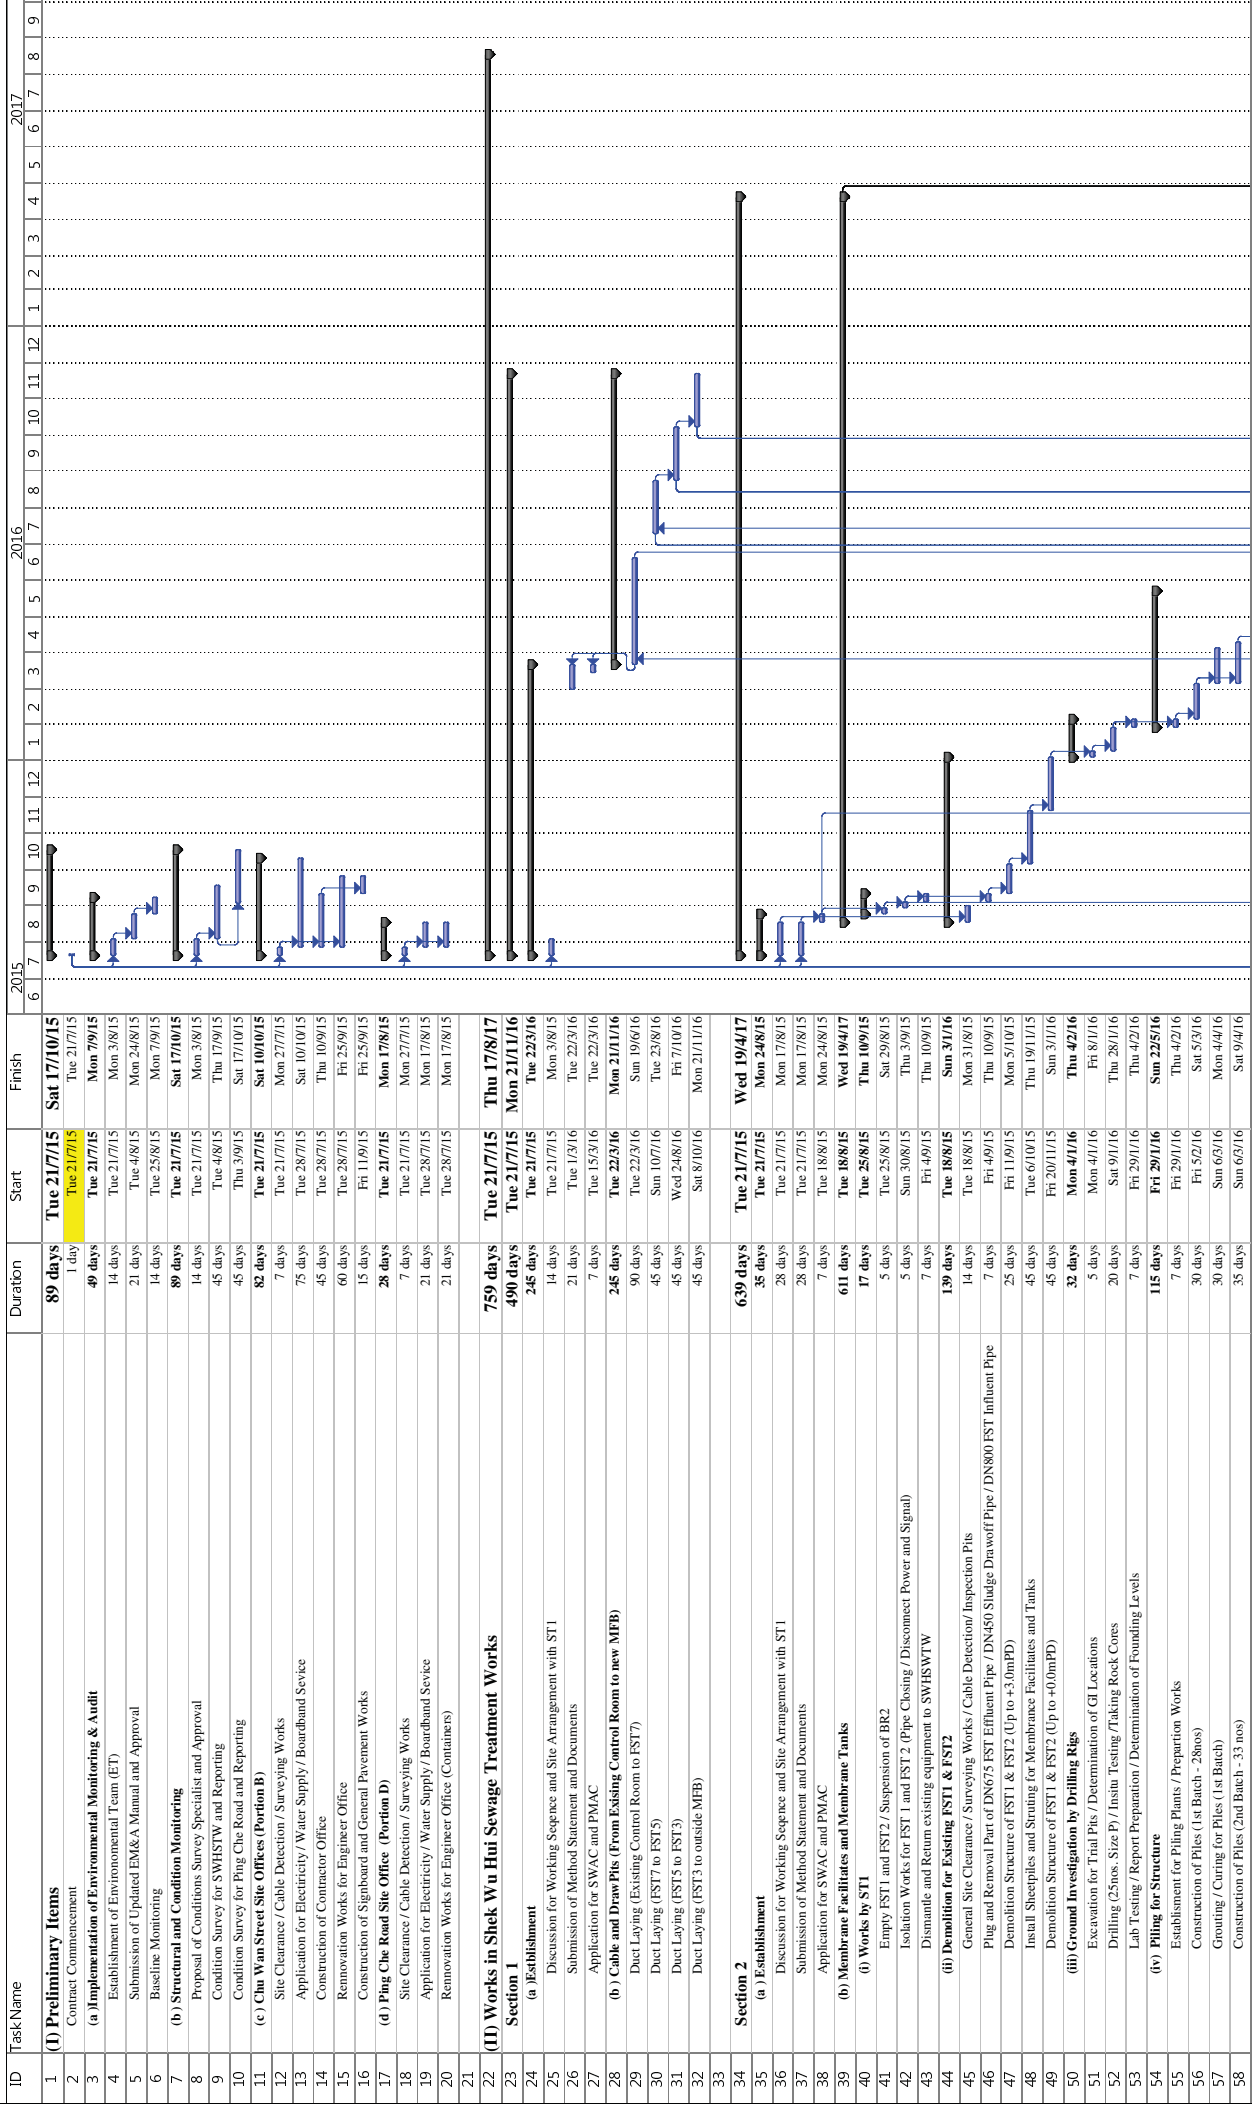


Contract DC/2013/09  
Advance Works for Shek Wu Hui Sewage Treatment Works -  
Further Expansion Phase 1A and Sewage Works at Ping Che Road  
Works Programme (Sep 2015)

ID	Task Name	Duration	Start	Finish	2015	2016	2017
59	Grouting / Curing for Piles (2nd Batch)	30 days	Sun 10/4/16	Mon 9/5/16			
60	<b>Pile Setting and Proof drilling</b>	<b>25 days</b>	<b>Thu 28/4/16</b>	<b>Sun 22/5/16</b>			
61	Setting-up of Pile-Load Test System (1st & 2nd pile)	7 days	Thu 28/4/16	Thu 5/5/16			
62	Pile-Load Test for Main Piles (1st and 2nd pile)	3 days	Fri 6/5/16	Mon 9/5/16			
63	Removal and Resetting of Pile-Load Test System	5 days	Tue 10/5/16	Sat 14/5/16			
64	Pile-Load Test for Main Pile (3rd and 4 pile)	3 days	Sun 15/5/16	Tue 17/5/16			
65	Removal of Pile-Load Test System	5 days	Wed 18/5/16	Sun 22/5/16			
66	Proof Drilling	5 days	Sun 15/5/16	Thu 19/5/16			
67	<b>(v) Construction of Substructure</b>	<b>155 days</b>	<b>Mon 23/5/16</b>	<b>Mon 24/10/16</b>			
68	<b>Portion A - Grid C-E / Grid F-G / Grid G-H - G-28</b>	<b>110 days</b>	<b>Mon 23/5/16</b>	<b>Fri 9/9/16</b>			
69	Excavation to Formation Level (+0.3/+2.4mPD)	15 days	Mon 23/5/16	Mon 6/6/16			
70	Laying Blinding Layer	2 days	Tue 7/6/16	Wed 8/6/16			
71	Preparation for Pilehead	5 days	Thu 9/6/16	Mon 13/6/16			
72	Steelfixing for Membrane Facilities (up to +1.9mPD) and Membrane Tank (up to +3.9mPD)	10 days	Tue 14/6/16	Thu 23/6/16			
73	Installation of formwork / waterstop / other accessory	7 days	Fri 24/6/16	Thu 30/6/16			
74	Concreting	3 days	Fri 17/7/16	Sun 3/7/16			
75	Curing of concrete / formwork removal / making good works	3 days	Mon 4/7/16	Wed 6/7/16			
76	Steelfixing for Membrane Facilities & Tanks (up to +5.4/+7.5mPD)	15 days	Thu 7/7/16	Thu 21/7/16			
77	Installation of formwork / waterstop / other accessory	10 days	Fri 22/7/16	Sun 31/7/16			
78	Concreting	3 days	Mon 18/7/16	Wed 3/8/16			
79	Curing of concrete / formwork removal / making good works	5 days	Thu 4/8/16	Mon 8/8/16			
80	Steelfixing for Membrane Facilities & Tanks (up to +6.77/5mPD)	15 days	Tue 9/8/16	Tue 23/8/16			
81	Installation of formwork / waterstop / other accessory	10 days	Wed 24/8/16	Fri 2/9/16			
82	Concreting	2 days	Sat 3/9/16	Sun 4/9/16			
83	Curing of concrete / formwork removal / making good works	5 days	Mon 5/9/16	Fri 9/9/16			
84	<b>Portion B - Grid A-C / Grid E-F / Grid G-H - G-14</b>	<b>115 days</b>	<b>Tue 7/6/16</b>	<b>Thu 29/9/16</b>			
85	Excavation to Formation Level (+0.3/+2.4mPD)	20 days	Tue 7/6/16	Sun 26/6/16			
86	Laying Blinding Layer	2 days	Mon 27/6/16	Tue 28/6/16			
87	Preparation for Pilehead	5 days	Wed 29/6/16	Sun 3/7/16			
88	Steelfixing for Membrane Facilities (up to +1.9mPD) and Membrane Tank (up to +3.9mPD)	10 days	Mon 4/7/16	Wed 13/7/16			
89	Installation of formwork / waterstop / other accessory	7 days	Thu 14/7/16	Wed 20/7/16			
90	Concreting	3 days	Thu 21/7/16	Sat 23/7/16			
91	Curing of concrete / formwork removal / making good works	3 days	Sun 24/7/16	Tue 26/7/16			
92	Steelfixing for Membrane Facilities & Tanks (up to +5.4/+7.5mPD)	15 days	Wed 27/7/16	Wed 10/8/16			
93	Installation of formwork / waterstop / other accessory	10 days	Thu 11/8/16	Sat 20/8/16			
94	Concreting	3 days	Sun 21/8/16	Tue 23/8/16			
95	Curing of concrete / formwork removal / making good works	5 days	Wed 24/8/16	Sun 28/8/16			
96	Steelfixing for Membrane Facilities & Tanks (up to +6.77/5mPD)	15 days	Mon 29/8/16	Mon 12/9/16			
97	Installation of formwork / waterstop / other accessory	10 days	Tue 13/9/16	Thu 22/9/16			
98	Concreting	2 days	Fri 23/9/16	Sat 24/9/16			
99	Curing of concrete / formwork removal / making good works	5 days	Sun 25/9/16	Thu 29/9/16			
100	Backfilling and Extracting Sheephile	25 days	Fri 30/9/16	Mon 24/10/16			
101	<b>(v) Construction of Superstructure</b>	<b>187 days</b>	<b>Fri 30/9/16</b>	<b>Tue 4/4/17</b>			
102	Erect Working Platform and Falsework (up to +11.65mPD)	15 days	Fri 30/9/16	Fri 14/10/16			
103	Steelfixing for Membrane Facilities Bldgs	15 days	Sat 15/10/16	Sat 29/10/16			
104	Installation of formwork / other accessory	15 days	Sun 30/10/16	Sun 13/11/16			
105	Concreting	2 days	Mon 14/11/16	Tue 15/11/16			
106	Curing of concrete / formwork removal / making good works	7 days	Wed 16/11/16	Tue 22/11/16			
107	Steelfixing for Membrane Facilities Bldgs (up tp +12.95mPD)	10 days	Wed 23/11/16	Fri 2/12/16			
108	Installation of formwork / other accessory	7 days	Sat 3/12/16	Fri 9/12/16			
109	Concreting	2 days	Sat 10/12/16	Sun 11/12/16			
110	Curing of concrete / formwork removal / making good works	5 days	Mon 12/12/16	Fri 16/12/16			
111	Steelfixing for Membrane Facilities Bldgs (up tp +14.45mPD)	10 days	Sat 17/12/16	Mon 26/12/16			
112	Installation of formwork / other accessory	7 days	Tue 27/12/16	Mon 2/1/17			
113	Concreting	2 days	Tue 3/1/17	Wed 4/1/17			
114	Curing of concrete / formwork removal / making good works	5 days	Thu 5/1/17	Mon 9/1/17			
115	Erect Working Platform and Falsework (up to +19.2mPD)	15 days	Thu 5/1/17	Thu 19/1/17			
116	Steelfixing for Membrane Facilities Bldgs (up tp +19.2mPD)	15 days	Fri 20/1/17	Fri 3/2/17			



Contract DC/2013/09  
Advance Works for Shek Wu Hui Sewage Treatment Works -  
Further Expansion Phase 1A and Sewage Works at Ping Che Road  
Works Programme (Sep 2015)

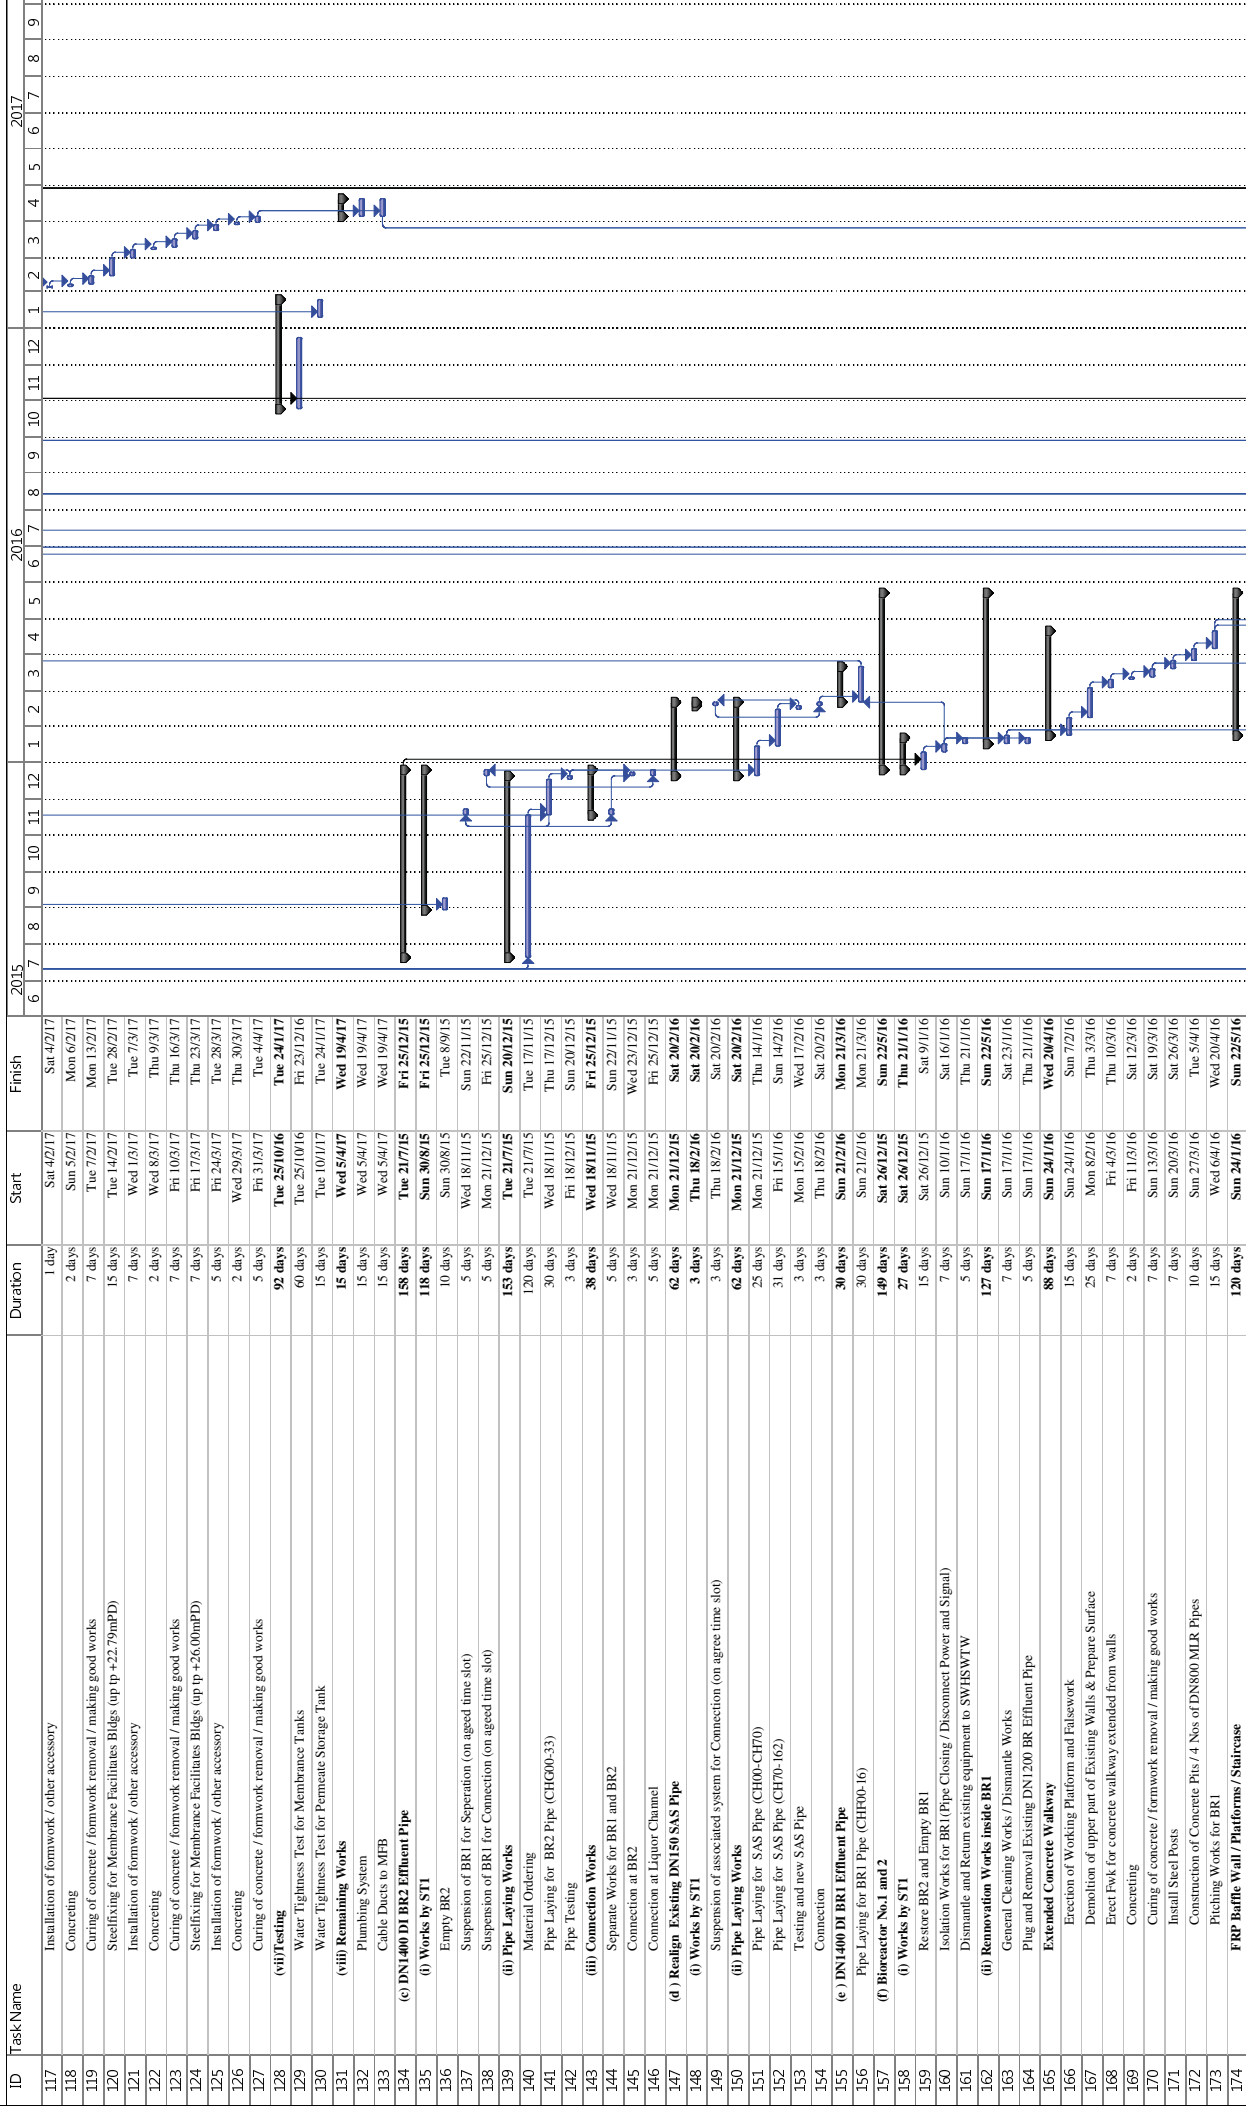

**Contract DC/2013/09**  
**Advance Works for Shek Wu Hui Sewage Treatment Works -**  
**Further Expansion Phase 1A and Sewage Works at Ping Che Road**  
**Works Programme (Sep 2015)**

ID	Task Name	Duration	Start	Finish	2015	2016	2017
175	Design, Supply & Installation	120 days	Sun 24/7/16	Sun 22/5/16			
176	(iii) <b>BR1 MS Air Mains within BR1</b>	25 days	Sun 20/3/16	Wed 13/4/16			
177	Pipe Laying for BR1 Pipe (CHD96-158 & CHD00-62)	15 days	Sun 20/3/16	Sun 3/4/16			
178	Pipe Laying for BR1 Pipe (CHD61-96)	10 days	Mon 4/4/16	Wed 13/4/16			
179	(g) <b>Pretreatment Screen Chamber &amp; Flow Meter Chamber</b>	168 days	Mon 18/4/16	Sun 27/10/16			
180	(i) <b>Works by ST1</b>	168 days	Mon 18/4/16	Sun 27/10/16			
181	Isolation Works for associated Pipeworks (Pipe Closing / Disconnect Power and Signal)	3 days	Mon 18/4/16	Wed 20/4/16			
182	Suspension of Sludge Draw Off Chamber No.1 and Distribution Chamber No.1	2 days	Sat 17/10/16	Sun 27/10/16			
183	(ii) <b>Construction of Pretreatment Screen Chamber &amp; Flow Meter Chamber</b>	66 days	Thu 21/4/16	Sat 25/6/16			
184	Excavation and ELS Installation	10 days	Thu 21/4/16	Sat 30/4/16			
185	Demolish existing pipeworks and Treatment for connection	2 days	Sun 15/5/16	Mon 2/5/16			
186	Lay Rockfills and Blinding	3 days	Tue 3/5/16	Thu 5/5/16			
187	Steel Fixing for Chambers (up to +4.5mPD)	3 days	Fri 6/5/16	Sun 8/5/16			
188	Installation of formwork / waterstop / other accessory	3 days	Mon 9/5/16	Wed 11/5/16			
189	Concreting	2 days	Thu 12/5/16	Fri 13/5/16			
190	Curing of concrete / formwork removal / making good works	2 days	Sat 14/5/16	Sun 15/5/16			
191	Steel Fixing for Chambers (up to +8.55 / +7.3mPD)	5 days	Mon 16/5/16	Fri 20/5/16			
192	Installation of formwork / waterstop / other accessory	5 days	Sat 21/5/16	Wed 25/5/16			
193	Concreting	2 days	Thu 26/5/16	Fri 27/5/16			
194	Curing of concrete / formwork removal / making good works	7 days	Sat 28/5/16	Fri 3/6/16			
195	Remove Sheetpiles and Backfilling	7 days	Sat 4/6/16	Fri 10/6/16			
196	Construction of Associated valve Pits	15 days	Sat 11/6/16	Sat 25/6/16			
197	(iii) <b>DN100 Screen Wash Water Pipe / DN 80 Screen Slip Wash Water Pipe</b>	50 days	Sun 14/8/16	Sun 21/10/16			
198	Pipe Laying for Pipe (CHD00-55 & CHD00-68)	45 days	Sun 14/8/16	Tue 27/9/16			
199	Testing	3 days	Wed 28/9/16	Fri 30/9/16			
200	Connection	2 days	Sat 11/10/16	Sun 21/10/16			
201	(h) <b>DN1400 DI RAS Pipe</b>	216 days	Sun 26/6/16	Fri 27/11/17			
202	Construction of Concrete Pipe Trough (beside BR1)	44 days	Sun 26/6/16	Mon 8/8/16			
203	Excavation and Sheetpiling	15 days	Sun 26/6/16	Sun 10/7/16			
204	Lay Rockfill and Blinding	2 days	Mon 11/7/16	Tue 12/7/16			
205	Steel Fixing for Base	3 days	Wed 13/7/16	Fri 15/7/16			
206	Installation of formwork / waterstop / other accessory	3 days	Sat 16/7/16	Mon 18/7/16			
207	Concreting	2 days	Tue 19/7/16	Wed 20/7/16			
208	Curing of concrete / formwork removal / making good works	2 days	Thu 21/7/16	Fri 22/7/16			
209	Steel Fixing for Wall	3 days	Sat 23/7/16	Mon 25/7/16			
210	Installation of formwork / waterstop / other accessory	3 days	Tue 26/7/16	Thu 28/7/16			
211	Concreting	2 days	Fri 29/7/16	Sat 30/7/16			
212	Curing of concrete / formwork removal / making good works	2 days	Sun 31/7/16	Mon 1/8/16			
213	Remove Sheetpiles and Backfilling	7 days	Tue 2/8/16	Mon 8/8/16			
214	Pipe Laying for RAS Pipe ( CHC08-153)	5 days	Tue 9/8/16	Sat 13/8/16			
215	Pipe Laying for RAS Pipe ( CHC75-98)	20 days	Tue 25/10/16	Sun 13/11/16			
216	Pipe Laying for RAS Pipe ( CHC35-75)	30 days	Mon 14/11/16	Tue 13/12/16			
217	Pipe Laying for RAS Pipe ( CHC00-35)	45 days	Wed 14/12/16	Fri 27/11/17			
218	(i) <b>BR1 MS Air Mains Outside BR1</b>	50 days	Tue 25/10/16	Tue 13/12/16			
219	Pipe Laying for BR1 Pipe (CHD4-61)	20 days	Tue 25/10/16	Sun 13/11/16			
220	Pipe Laying for BR1 Pipe (CHD00-44)	30 days	Mon 14/11/16	Tue 13/12/16			
221	(j) <b>CLP Cable and Drawpits</b>	304 days	Mon 20/6/16	Wed 19/4/17			
222	CLP Cable Ducts with Trench (Outside to FST7)	20 days	Mon 20/6/16	Sat 9/7/16			
223	CLP Cable Ducts with Trench (FST7 to FST3)	45 days	Sun 10/7/16	Tue 23/8/16			
224	CLP Cable Ducts with Trench (FST5 to FST3)	45 days	Wed 24/8/16	Fri 7/10/16			
225	CLP Cable Ducts with Trench (FST3 to Outside MFB)	45 days	Sat 8/10/16	Mon 21/11/16			
226	CLP Cable Ducts with Trench (to MFB)	15 days	Wed 5/4/17	Wed 19/4/17			
227	(k) <b>Fresh Watermains and Fire Service Watermains</b>	304 days	Mon 20/6/16	Wed 19/4/17			
228	PipeLaying (Outside to FST7)	20 days	Mon 20/6/16	Sat 9/7/16			
229	PipeLaying (FST7 to FST5)	45 days	Sun 10/7/16	Tue 23/8/16			
230	PipeLaying (FST5 to FST3)	45 days	Wed 24/8/16	Fri 7/10/16			
231	PipeLaying (FST3 to Outside MFB )	45 days	Sat 8/10/16	Mon 21/11/16			
232	PipeLaying (toMFB )	15 days	Wed 5/4/17	Wed 19/4/17			

Task

Milestone


Summary

Date: 15 Sep 2015

Page 4

Revision 02

**Contract DC/2013/09**  
**Advance Works for Shek Wu Hui Sewage Treatment Works -**  
**Further Expansion Phase 1A and Sewage Works at Ping Che Road**  
**Works Programme (Sep 2015)**

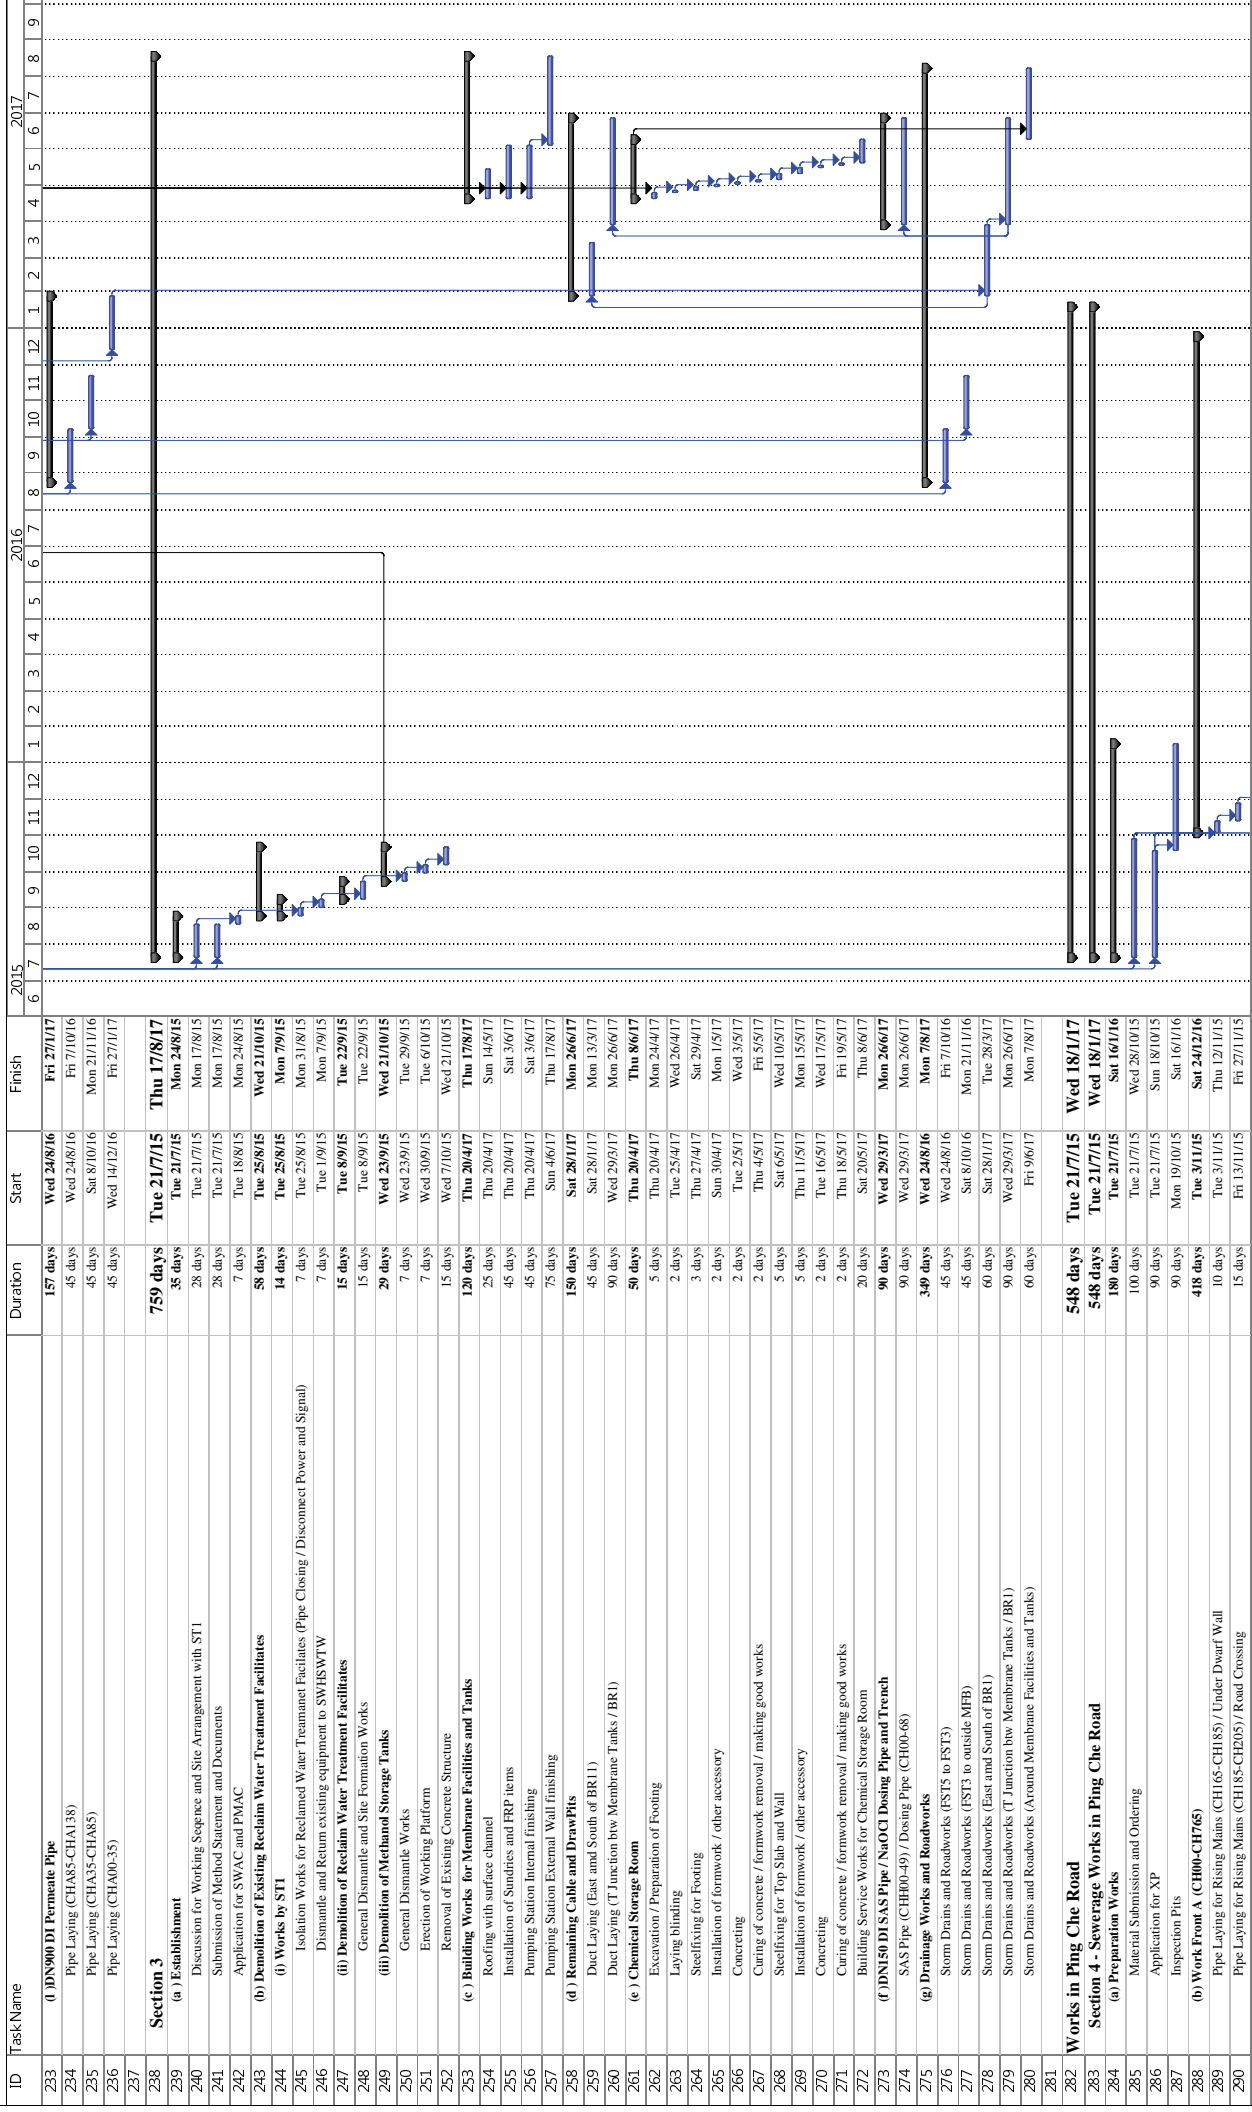


Contract DC/2013/09  
Advance Works for Shek Wu Hui Sewage Treatment Works -  
Further Expansion Phase 1A and Sewage Works at Ping Che Road  
Works Programme (Sep 2015)

ID	Task Name	Duration	Start	Finish	2015	2016	2017
291	Pipe Laying for Rising Mains (CH205-CH245) / Under Dwarf Wall	20 days	Sat 28/11/15	Thu 17/12/15	6	7	8
292	Pipe Laying for Rising Mains (CH245-CH295) / Footpath	18 days	Fri 18/12/15	Mon 4/1/16	7	8	9
293	Pipe Laying for Rising Mains (CH295-CH300) / Road Crossing	10 days	Tue 5/1/16	Thu 14/1/16	8	9	
294	Pipe Laying for Rising Mains (CH300-CH360) / Footpath	20 days	Fri 15/1/16	Wed 3/2/16	9	10	
295	Pipe Laying for Rising Mains (CH360-CH425) / Under Dwarf Wall	35 days	Thu 4/2/16	Wed 9/3/16	10	11	
296	Pipe Laying for Rising Mains (CH425-CH445) / Road Crossing	15 days	Thu 10/3/16	Thu 24/3/16	11	12	
297	Pipe Laying for Rising Mains (CH445-CH560) / Under Dwarf Wall	58 days	Fri 25/3/16	Sat 21/5/16	12	1	
298	Interim Pressure Test	7 days	Sun 22/5/16	Sat 28/5/16	1	2	
299	Pipe Laying for Rising Mains (CH560-CH590) / Footpath	15 days	Sun 29/5/16	Sun 12/6/16	2	3	
300	Pipe Laying for Rising Mains (CH590-CH660) / Under Dwarf Wall	35 days	Mon 13/6/16	Sun 17/7/16	3	4	
301	Pipe Laying for Rising Mains (CH660-CH670) / Road Crossing	15 days	Mon 18/7/16	Mon 1/8/16	4	5	
302	Pipe Laying for Rising Mains (CH670-CH750) / Under Dwarf Wall	40 days	Tue 2/8/16	Sat 1/9/16	5	6	
303	Pipe Laying for Rising Mains (CH750-CH765) / Road Crossing	15 days	Sun 11/9/16	Sun 25/9/16	6	7	
304	Pipe Laying for Rising Mains (CH155-CH165) / Road Crossing	15 days	Mon 26/9/16	Mon 10/10/16	7	8	
305	Pipe Laying for Rising Mains (CH160-CH155) / Carpark	48 days	Tue 11/10/16	Sun 27/11/16	8	9	
306	Pipe Laying for Rising Mains (CH100-CH160) / Footpath	20 days	Mon 28/11/16	Sat 17/12/16	9	10	
307	Interim Pipe Testing	7 days	Sun 18/12/16	Sat 24/12/16	10	11	
308	(c) Work Front B (CH765-CH1540)	443 days	Tue 31/1/15	Wed 18/1/17	6	7	
309	Pipe Laying for Rising Mains (CH970-CH980) / Under Dwarf Wall	5 days	Tue 3/11/15	Sat 7/11/15	7	8	
310	Pipe Laying for Rising Mains (CH980-CH990) / Road Crossing	15 days	Sun 8/11/15	Sun 22/11/15	8	9	
311	Pipe Laying for Rising Mains (CH990-CH1000) / Under Dwarf Wall	5 days	Mon 23/11/15	Fri 27/11/15	9	10	
312	Pipe Laying for Rising Mains (CH1000-CH1010) / Road Crossing	15 days	Sat 28/11/15	Sat 12/12/15	10	11	
313	Pipe Laying for Rising Mains (CH1010-CH1085) / Under Dwarf Wall	23 days	Sun 13/12/15	Mon 4/1/16	11	12	
314	Pipe Laying for Rising Mains (CH1085-CH1075) / Road Crossing	15 days	Tue 5/1/16	Tue 19/1/16	12	1	
315	Pipe Laying for Rising Mains (CH1075-CH1095) / Under Dwarf Wall	10 days	Wed 20/1/16	Fri 29/1/16	1	2	
316	Pipe Laying for Rising Mains (CH1095-CH1180) / Footpath	28 days	Sat 30/1/16	Fri 26/2/16	2	3	
317	Pipe Laying for Rising Mains (CH1180-CH1205) / Road Crossing	20 days	Sat 27/2/16	Thu 17/3/16	3	4	
318	Pipe Laying for Rising Mains (CH1205-CH1270) / Under Dwarf Wall	33 days	Fri 18/3/16	Tue 19/4/16	4	5	
319	Pipe Laying for Rising Mains (CH1270-CH1290) / Road Crossing	15 days	Wed 20/4/16	Wed 4/5/16	5	6	
320	Pipe Laying for Rising Mains (CH1290-CH1335) / River Crossing	20 days	Thu 5/5/16	Tue 24/5/16	6	7	
321	Pipe Laying for Rising Mains (CH1335-CH1385) / Under Dwarf Wall	25 days	Wed 25/5/16	Sat 18/6/16	7	8	
322	Interim Pipe Testing	7 days	Sun 19/6/16	Sat 25/6/16	8	9	
323	Pipe Laying for Rising Mains (CH1385-CH1410) / Road Crossing	15 days	Sun 26/6/16	Sun 10/7/16	9	10	
324	Pipe Laying for Rising Mains (CH1410-CH1430) / Under Dwarf Wall	10 days	Mon 11/7/16	Wed 20/7/16	10	11	
325	Pipe Laying for Rising Mains (CH1430-CH1440) / Footpath	5 days	Thu 21/7/16	Mon 25/7/16	11	12	
326	Pipe Laying for Rising Mains (CH1440-CH1495) / Under Dwarf Wall	25 days	Tue 26/7/16	Fri 19/8/16	12	1	
327	Pipe Laying for Rising Mains (CH1495-CH1520) / Footpath	10 days	Sat 20/8/16	Mon 29/8/16	1	2	
328	Pipe Laying for Rising Mains (CH1520-CH1540) / Under Dwarf Wall	10 days	Tue 30/8/16	Thu 8/9/16	2	3	
329	Pipe Laying for Rising Mains (CH950-CH970) / Road Crossing	15 days	Fri 9/9/16	Fri 23/9/16	3	4	
330	Pipe Laying for Rising Mains (CH855-CH950) / Under Dwarf Wall	48 days	Sat 24/9/16	Thu 10/11/16	4	5	
331	Pipe Laying for Rising Mains (CH845-CH855) / Road Crossing	15 days	Fri 11/11/16	Fri 25/11/16	5	6	
332	Pipe Laying for Rising Mains (CH765-CH845) / Under Dwarf Wall	40 days	Sat 26/11/16	Wed 4/1/17	6	7	
333	Final Pressure Testing and Swabbing	14 days	Thu 5/1/17	Wed 18/1/17	7	8	

## **Appendix E**

### **PROPOSED MONITORING LOCATIONS**

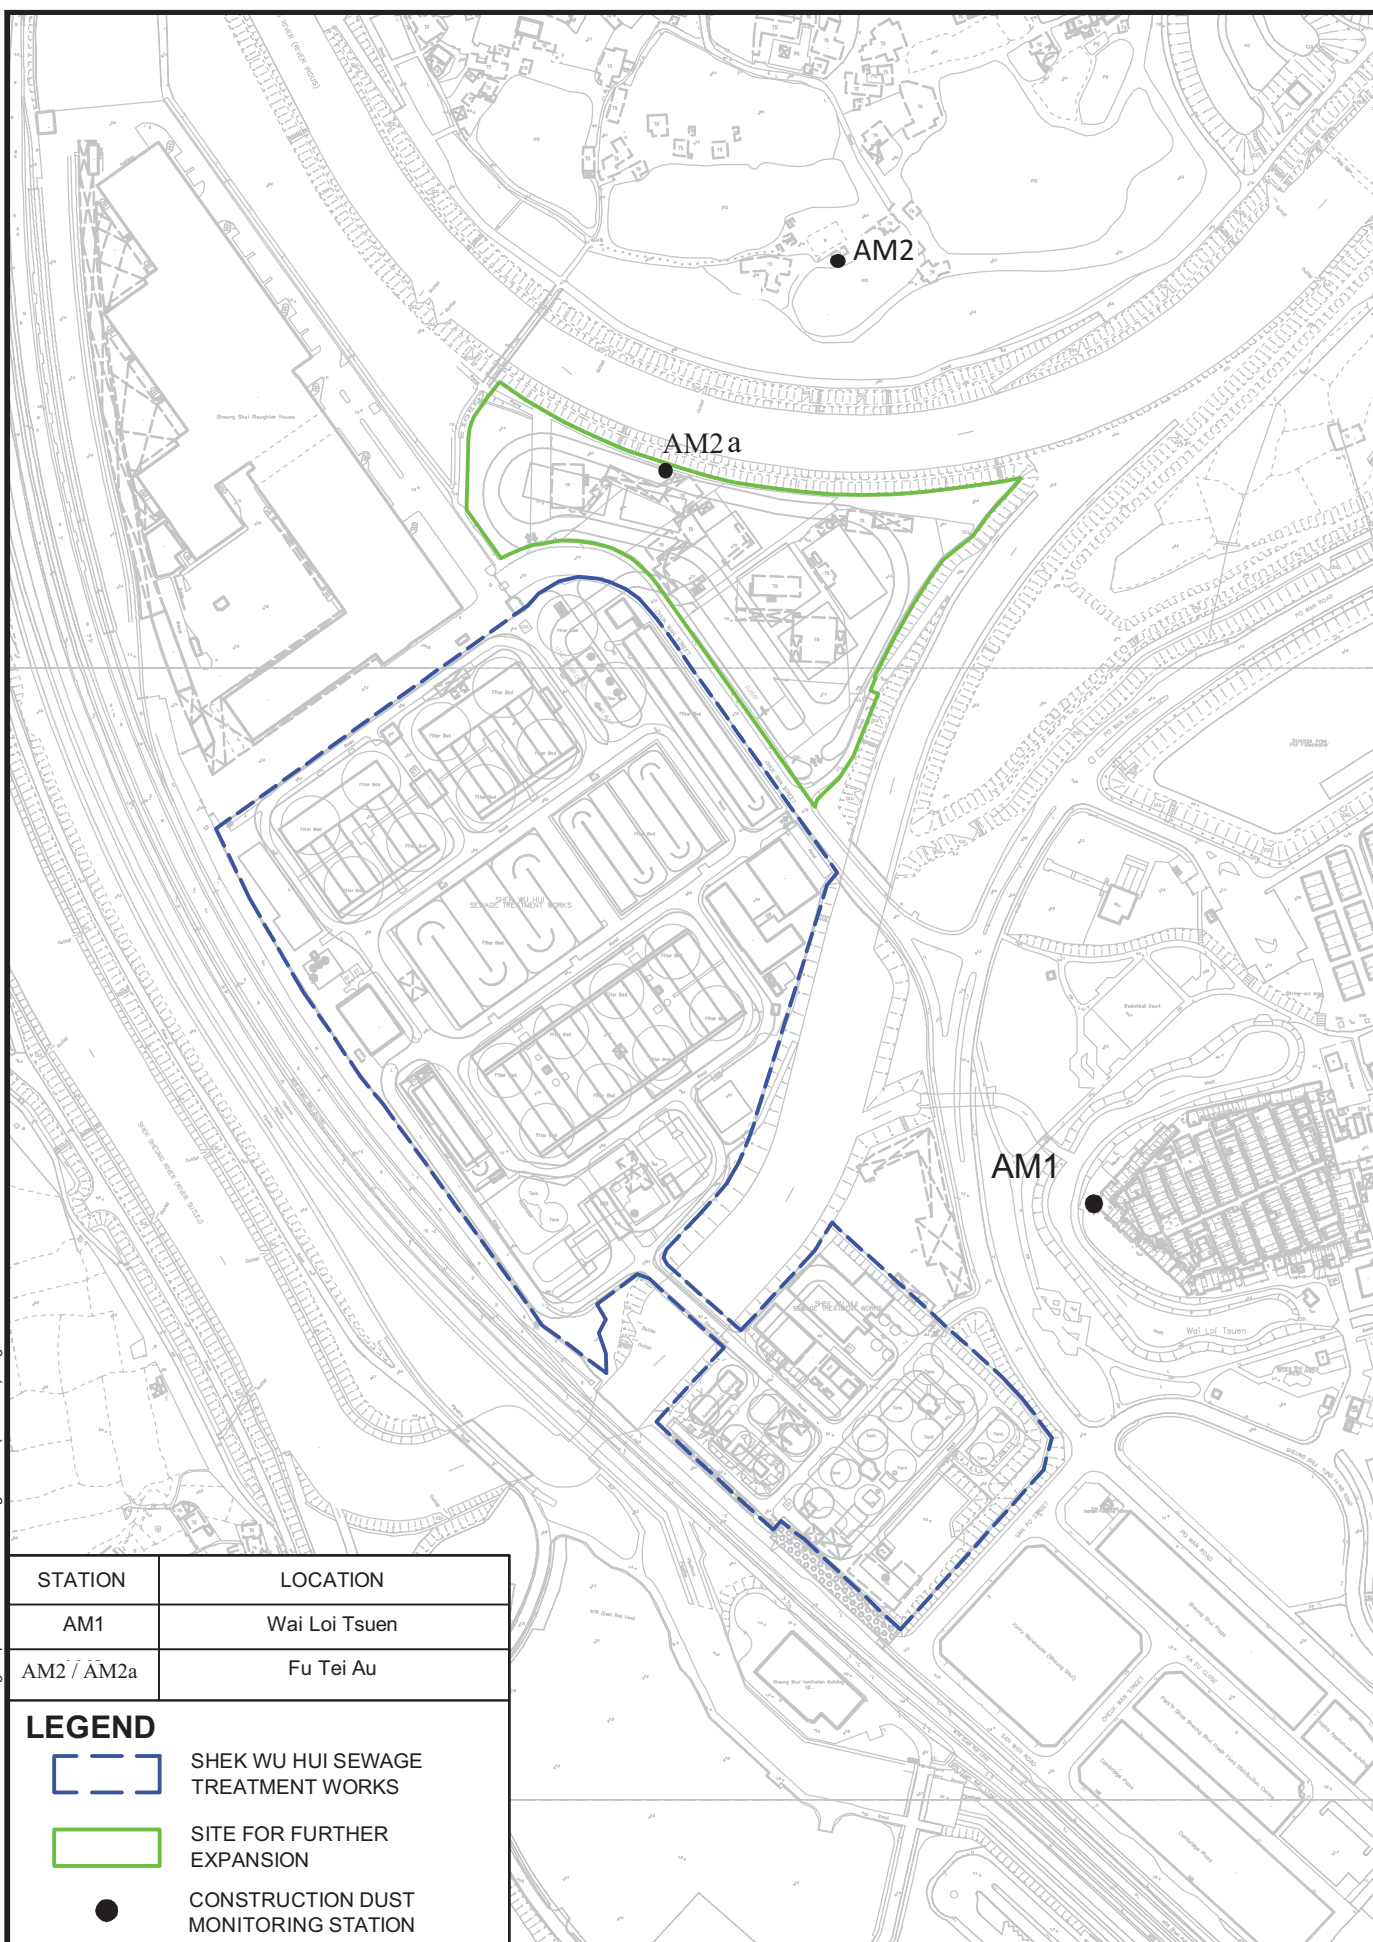

AGREEMENT NO. CE 40/2012 (DS)  
 SHEK WU HUI SEWAGE TREATMENT WORKS  
 - FURTHER EXPANSION PHASE 1A  
 - INVESTIGATION


PROPOSED CONSTRUCTION DUST MONITORING  
 STATIONS FOR CONSTRUCTION PHASE AND  
 OPERATION PHASE

**AECOM**

Project No.: 60284037 Date: FEB. 2014

Drawing No.  
 60284037/EM&AM/405



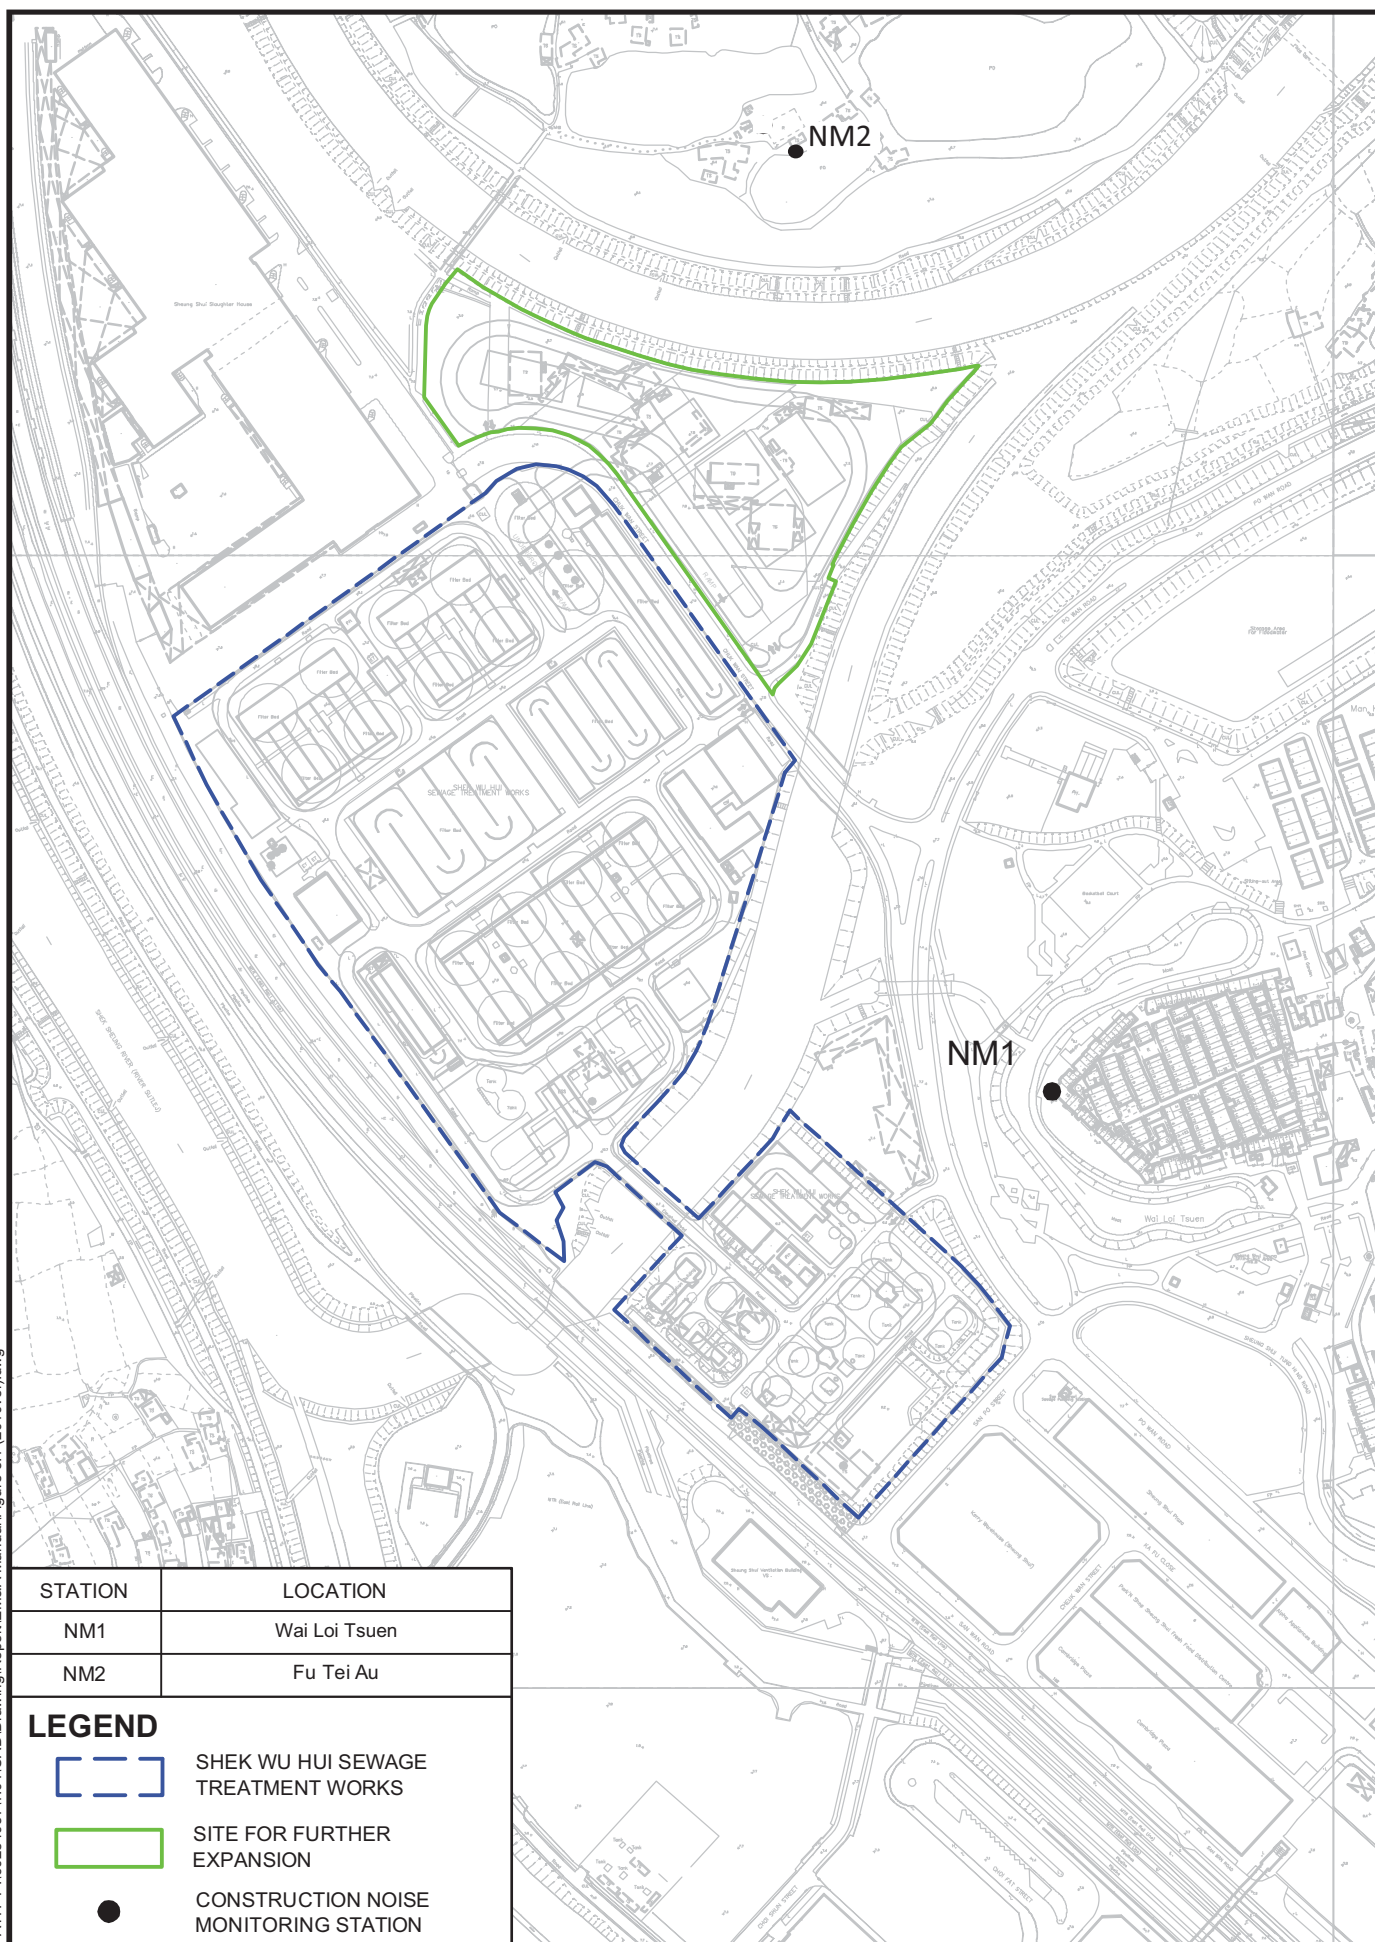

AGREEMENT NO. CE 40/2012 (DS)  
 SHEK WU HUI SEWAGE TREATMENT WORKS  
 - FURTHER EXPANSION PHASE 1A  
 - INVESTIGATION

# LOCATIONS OF CONSTRUCTION NOISE MONITORING STATIONS

**AECOM**

Project No.: 60284037 Date: FEB. 2014

Drawing No.  
 60284037/EM&AM/407



## **Appendix F**

### **EVENT ACTION PLAN**

**Event and Action Plan for Construction Dust**



Event	Action			
	ET	IEC	ER	Contractor
Action level being exceeded by one sampling	<ol style="list-style-type: none"> <li>1. Identify source, investigate the causes of complaint and propose remedial measures;</li> <li>2. Inform IEC and ER;</li> <li>3. Repeat measurement to confirm finding;</li> <li>4. Increase monitoring frequency to daily.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify Contractor.</li> </ol>	<ol style="list-style-type: none"> <li>1. Rectify any unacceptable practice;</li> <li>2. Amend working methods if appropriate.</li> </ol>
Action level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> <li>1. Identify source;</li> <li>2. Inform IEC and ER;</li> <li>3. Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>4. Repeat measurements to confirm findings;</li> <li>5. Increase monitoring frequency to daily;</li> <li>6. Discuss with IEC and Contractor on remedial actions required;</li> <li>7. If exceedance continues, arrange meeting with IEC and ER;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss with ET and Contractor on possible remedial measures;</li> <li>4. Advise the ET on the effectiveness of the proposed remedial measures;</li> <li>5. Supervise Implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. Ensure remedial measures properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit proposals for remedial actions to IEC within three working days of notification;</li> <li>2. Implement the agreed proposals;</li> <li>3. Amend proposal if appropriate.</li> </ol>
Limit level being exceeded by one sampling	<ol style="list-style-type: none"> <li>1. Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>2. Inform Contractor, IEC, ER, and EPD;</li> <li>3. Repeat measurement to confirm finding;</li> <li>4. Increase monitoring frequency to daily;</li> <li>5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss with ET and Contractor on possible remedial measures;</li> <li>4. Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>5. Supervise implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. Ensure remedial measures properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC within three working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Amend proposal if appropriate.</li> </ol>
Limit level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> <li>1. Notify IEC, ER, Contractor and EPD;</li> <li>2. Identify source;</li> <li>3. Repeat measurement to confirm findings;</li> <li>4. Increase monitoring frequency to daily;</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Ensure remedial measures properly implemented;</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC within three working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Resubmit proposals if problem still not under control;</li> <li>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>



**Event and Action Plan for Construction Noise**

Event	Action			
	ET	IEC	ER	Contractor
<b>Action Level</b>	<ol style="list-style-type: none"> <li>1. Notify IEC and Contractor;</li> <li>2. Carry out investigation;</li> <li>3. Report the results of investigation to the IEC, ER and Contractor;</li> <li>4. Discuss with the Contractor and formulate remedial measures;</li> <li>5. Increase monitoring frequency to check mitigation effectiveness.</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the analysed results submitted by the ET;</li> <li>2. Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>4. Ensure remedial measures are properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to IEC;</li> <li>2. Implement noise mitigation proposals.</li> </ol>
<b>Limit Level</b>	<ol style="list-style-type: none"> <li>1. Identify source;</li> <li>2. Inform IEC, ER, EPD and Contractor;</li> <li>3. Repeat measurements to confirm findings;</li> <li>4. Increase monitoring frequency;</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>6. Inform IEC, ER and EPD the causes and actions taken for the exceedances;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>4. Ensure remedial measures properly implemented;</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Resubmit proposals if problem still not under control;</li> <li>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>



## **Appendix G**

### **GRAPHICAL PLOTS**

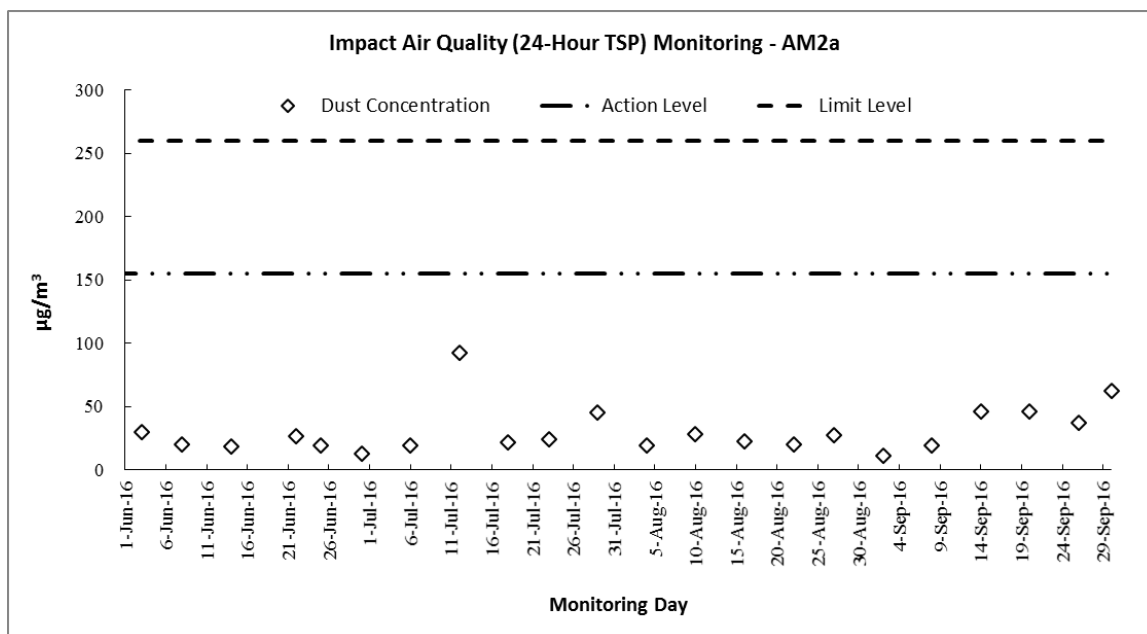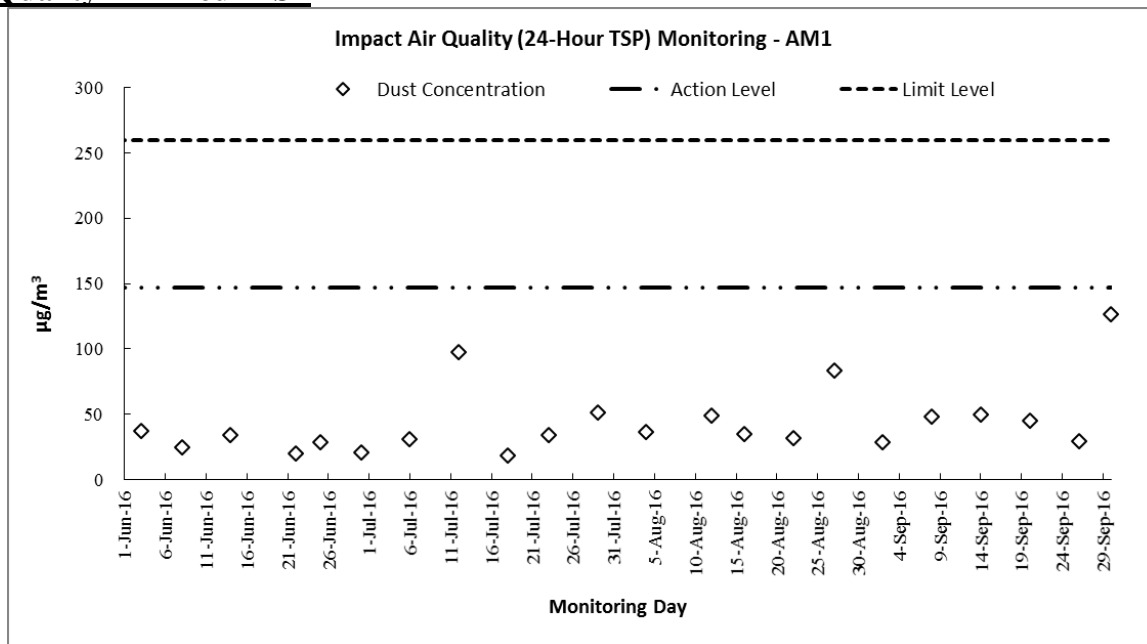**Air Quality – 24-Hour TSP**

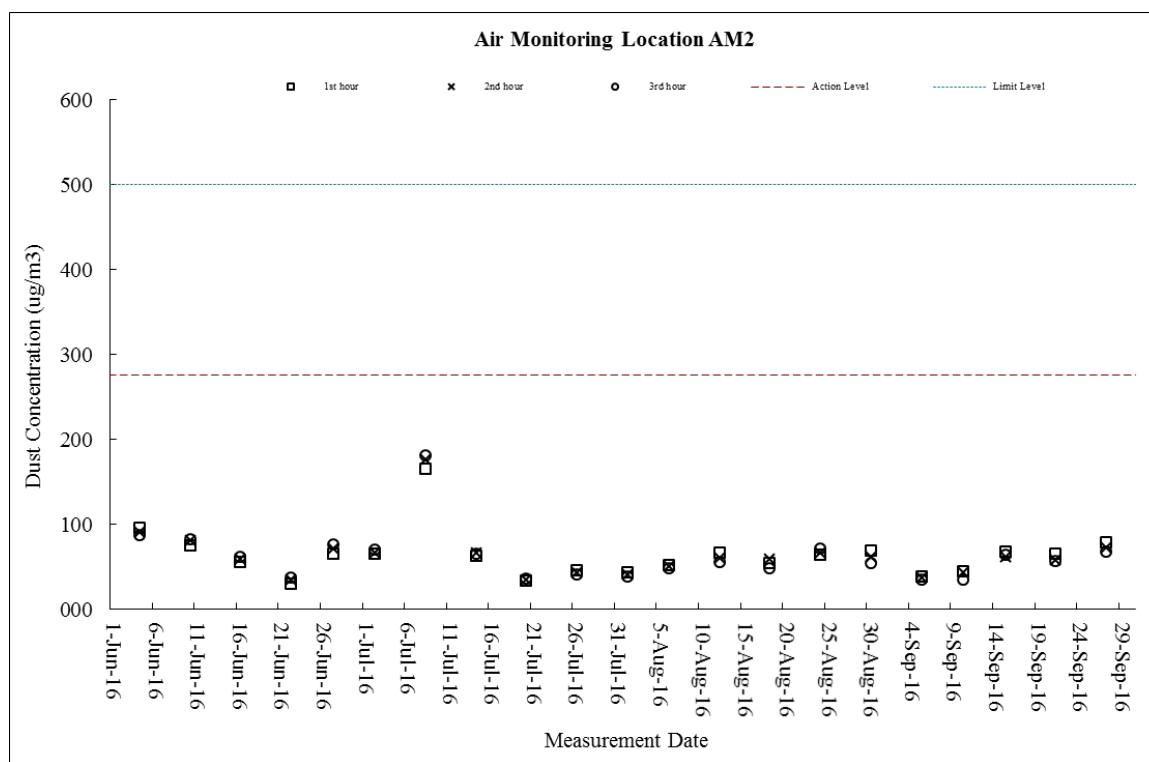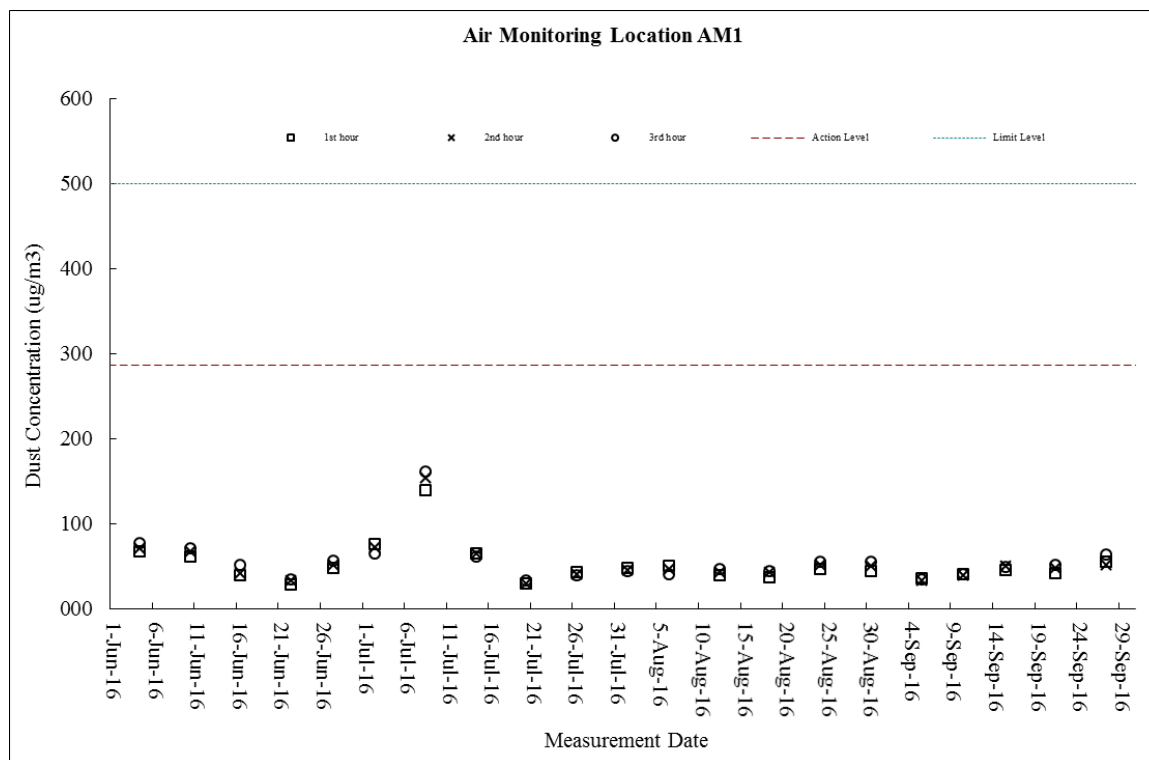**Air Quality – 1-Hour TSP**

## Construction Noise

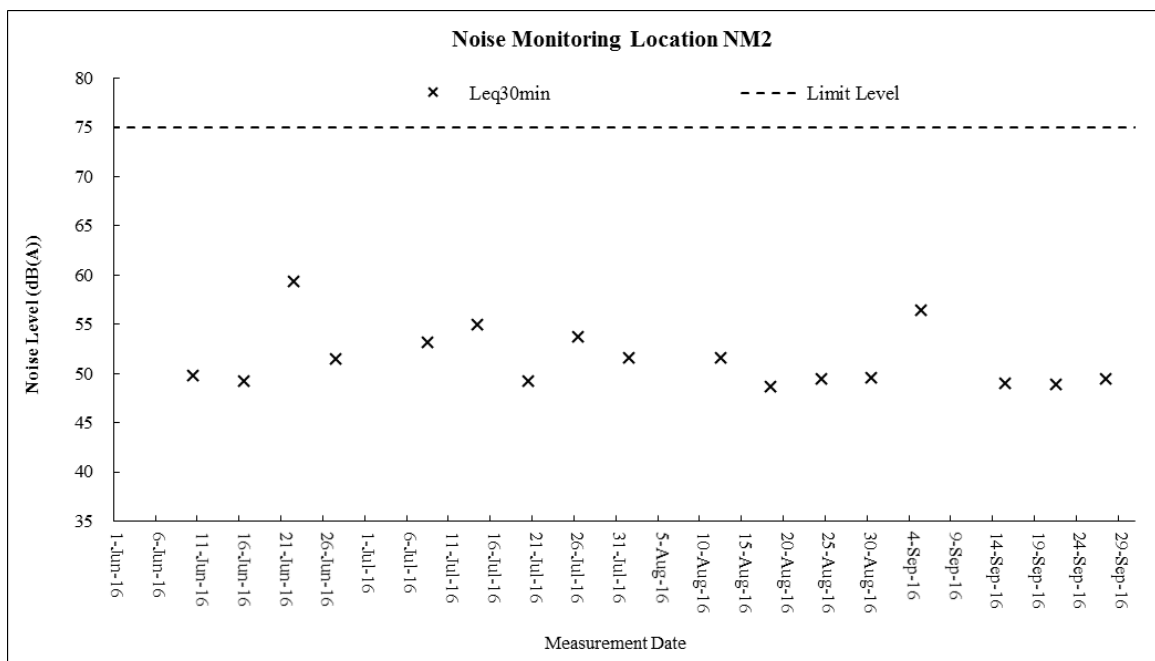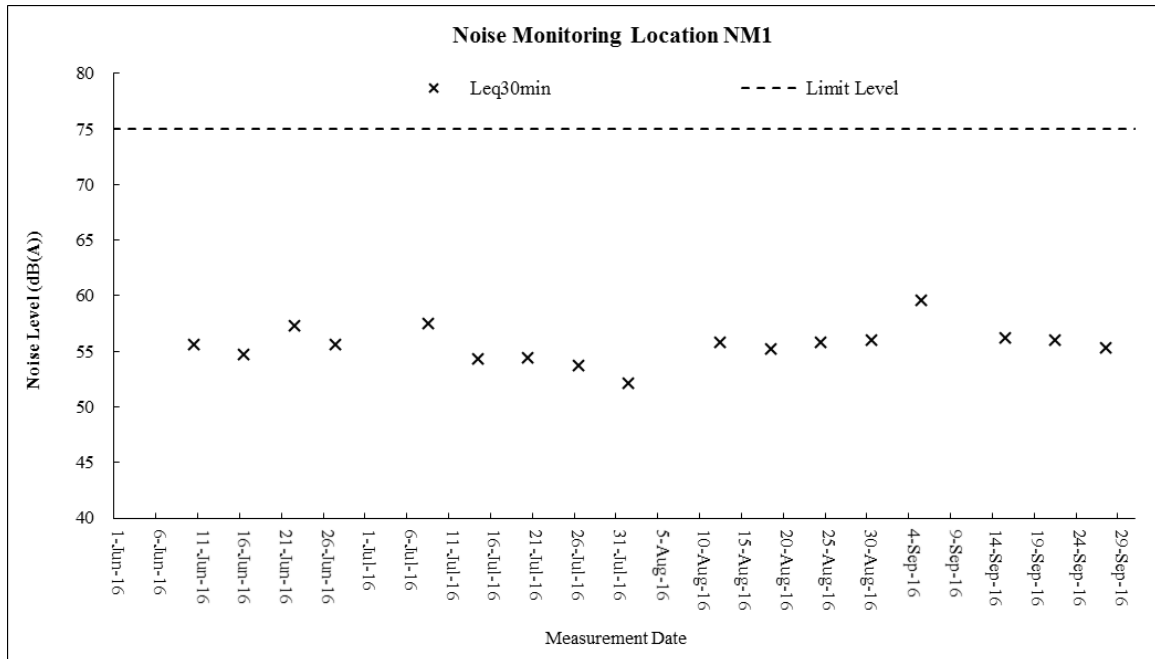



## **Appendix H**

### **METEOROLOGICAL INFORMATION**

### **The weather of July 2016**

With long spells of sunny skies under the dominance of the subtropical ridge, the weather was unusually hot in July 2016. The monthly mean temperature of 29.8 degrees was 1.0 degree higher than the normal figure of 28.8 degrees, equalling the previous highest record set in 2014. The month was much drier than usual with only 175.9 millimetres of rainfall, less than half of the July normal of 376.5 millimetres. The accumulated rainfall of 1408.7 millimetres for the first seven months was about 4 percent below the normal figure of 1473.3 millimetres for the same period.

### **The weather of August 2016**

The weather of August 2016 was generally rainy with less sunshine than usual. The total duration of sunshine recorded in the month was 148.5 hours, about 21 percent below the normal figure of 188.9 hours. The monthly total rainfall was 532.7 millimetres, about 23 percent above the normal figure of 432.2 millimetres. The accumulated rainfall of 1941.4 millimetres for the first eight months was about 2 percent above the normal figure of 1905.5 millimetres for the same period.

### **The weather of September 2016**

With rainy weather dominating the first part of the month, September 2016 was gloomier than usual. The total duration of sunshine recorded in the month was 135.7 hours, 36.6 hours below the normal figure of 172.3 hours and the seventh lowest on record for September. However, the month was slightly warmer than usual with a monthly mean temperature of 27.9 degrees, 0.2 degree higher than the normal figure of 27.7 degrees. The monthly total rainfall was 323.1 millimetres, slightly below the normal figure of 327.6 millimetres. The accumulated rainfall of 2264.5 millimetres for the first nine months was about 1 percent above the normal figure of 2233.1 millimetres for the same period.

## **Appendix I**

### **MONTHLY SUMMARY WASTE FLOW TABLE**

## Monthly Summary Waste Flow Table

Department: Drainage Services Department Contract No.: DC/2013/09  
 Contract Title: Advance Works for Shek Wu Hui Sewage Treatment Works - Further Expansion Phase 1A and Sewerage Works at Ping Che Road  
 Commencement Date: 21-Jul-2015 Estimated completion Date: 19-May-2017 Estimated Contract Sum: 1.56M

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )
Jan	0.335	0.111	0.060	0.000	0.164	0.000	0.000	0.000	0.000	0.000	0.000
Feb	2.377	0.089	0.050	2.228	0.010	0.000	0.000	0.000	0.000	0.000	0.008
Mar	0.141	0.015	0.050	0.000	0.076	0.000	0.000	0.000	0.000	0.000	0.007
Apr	0.160	0.010	0.050	0.000	0.100	0.000	0.000	0.000	0.000	0.000	0.023
May	0.334	0.000	0.010	0.000	0.324	0.000	0.000	0.000	0.000	0.000	0.026
June	2.517	0.024	0.300	0.000	2.193	0.000	0.000	0.000	0.000	0.000	0.013
<b>Sub-total</b>	<b>5.863</b>	<b>0.249</b>	<b>0.520</b>	<b>2.228</b>	<b>2.866</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.076</b>
July	3.284	0.000	0.150	0.000	3.134	0.000	0.000	0.000	0.000	0.000	0.002
Aug	0.396	0.005	0.100	0.000	0.291	0.000	4.720	0.000	0.000	0.000	0.012
Sep	0.529	0.000	0.100	0.000	0.429	0.000	0.000	0.000	0.000	0.000	0.008
Oct											
Nov											
Dec											
<b>Total</b>	<b>10.072</b>	<b>0.254</b>	<b>0.870</b>	<b>2.228</b>	<b>6.720</b>	<b>0.000</b>	<b>4.720</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.098</b>

- Notes: (1) The waste flow table should cover the whole construction period of the Contract.
- (2) The original estimates of the C&D materials should be the estimates at contract commencement and should not be altered during construction.
- (3) Inert C&D materials that are specified in the Contract to be imported for use at the Site shall be separately indicated.
- (4) The yearly estimates of the C&D materials should be updated as appropriate taking into account the latest works programme etc.
- (5) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.

## **Appendix J**

### **IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)**

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
<b>Air Quality Impact</b>						
S2.4.1.3	<p>Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices:</p> <ul style="list-style-type: none"> <li>Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading;</li> <li>Any dusty material remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads;</li> <li>A stockpile of dusty material should not be extended beyond the pedestrian barriers, fencing or traffic cones;</li> <li>The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle;</li> <li>Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;</li> <li>When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period.</li> <li>The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials;</li> <li>Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously;</li> <li>Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet;</li> </ul>	To minimize the dust impact	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Air Pollution Control Ordinance (APCO) and Air Pollution Control (Construction Dust) Regulation



EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
<b>Air Quality Impact</b>						
	<ul style="list-style-type: none"><li>• Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding;</li><li>• Any skip hoist for material transport should be totally enclosed by impervious sheeting;</li><li>• Every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;</li><li>• Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed;</li><li>• Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system; and</li><li>• Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabilizer within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.</li></ul>					

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
<b>Noise Impact</b>						
S3.4.1.1	Use of movable barrier, enclosure, acoustic mat and quiet plant. Use of wooden frames barrier with a small-cantilevered upper portion of superficial density not less than 14kg/m <sup>2</sup> on a skid footing with 25mm thick internal sound absorptive lining.	To minimize construction noise impact arising from the Project at the affected noise sensitive receivers (NSRs)	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM, Noise Control Ordinance (NCO)
S3.4.1.2	<p>Good Site Practice:</p> <ul style="list-style-type: none"> <li>• Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program.</li> <li>• Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program.</li> <li>• Mobile plant, if any, should be sited as far away from NSRs as possible.</li> <li>• Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum.</li> <li>• Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.</li> <li>• Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities.</li> </ul>	To minimize construction noise impact arising from the Project at the affected NSRs	Contractor	Work Sites	Construction period of Advance Works and Main Works of Phase 1A	EIAO-TM, NCO

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
<b>Ecological Impact</b>						
S4.2.1.1	Solid dull green noise/visual barriers of at least 2m high shall be erected and maintained between active works area and all areas of ecological importance.	Minimize noise and human disturbances during construction phase.	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM
S4.2.1.2	Avoid unnecessary lighting.	Minimize mortality impacts on birds.	Design Contractor / Plant Operator	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM
S4.2.1.3	Good construction site practice to minimise dust generation should be followed on all construction sites. Measures to avoid, minimise and mitigate impacts on air quality are detailed in this schedule	Minimize dust generation from construction sites.	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM
S4.2.1.4	<p>The following measures to avoid, minimise and mitigate impact on water quality during construction phase shall be implemented</p> <ul style="list-style-type: none"> <li>• Temporary sewerage and drainage to be designed and installed to collect wastewater and prevent it from entering water bodies;</li> <li>• Proper locations well away from nearby water bodies should be used for temporary storage of materials (i.e. equipment, filling materials, chemicals and fuel) and temporary stockpiles of construction debris and spoil, and these should be identified before commencement of works;</li> <li>• To prevent muddy water entering nearby water bodies, work sites close to nearby water bodies should be isolated, using such items as sandbags or silt curtains with lead edge at bottom and properly supported props. Other protective measures should also be taken to ensure that no pollution or siltation occurs to the water gathering grounds of the work sites;</li> <li>• Construction debris and spoil should be covered and/or properly disposed of as soon as possible to avoid these being washed into nearby water bodies;</li> <li>• Proper locations for discharge outlets of temporary wastewater treatment facilities well away from sensitive receivers should be identified;</li> </ul>	Avoid, minimise and mitigate impact on water quality	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
<b>Ecological Impact</b>						
	<ul style="list-style-type: none"> <li>• Adequate lateral support should be erected where necessary in order to prevent soil/mud from slipping into water bodies;</li> <li>• Site boundaries should be clearly marked and any works beyond the boundary strictly prohibited;</li> <li>• Regular water monitoring and site audit should be carried out at adequate points along any watercourses where construction works are underway upstream within their catchments and also on the Ng Tung, Sheung Yue and Shek Sheung Rivers. If the monitoring and audit results show that pollution occurs, adequate measures including temporarily cessation of works should be considered;</li> <li>• Excavation profiles should be properly designed and executed with attention to the relevant requirements for environment, health and safety;</li> <li>• Where soil to be excavated is situated beneath the groundwater table, it may be necessary to lower the groundwater table by installing well points or similar means;</li> <li>• Stockpiling sites should be lined with impermeable sheeting and banded. Stockpiles should be properly covered by impermeable sheeting to reduce dust emission during dry season or contaminated run-off during rainy season. Watering should be avoided on stockpiles of contaminated soil to minimize contaminated runoff and construction materials should be properly covered and located away from nearby water bodies; and</li> <li>• Supply of suitable clean backfill material after excavation, if required.</li> <li>• Vehicles containing any excavated materials should be suitably covered to limit potential dust emissions or contaminated run-off, and truck bodies and tailgates should be sealed to prevent discharge during transport or during wet season;</li> <li>• Speed control for the trucks carrying contaminated materials should be enforced;</li> <li>• Vehicle wheel washing facilities at construction sites' exit points should be established and used, where necessary; and</li> <li>• Other measures as detailed in this schedule.</li> </ul>					

<b>EM&amp;A Ref.</b>	<b>Recommended Mitigation Measures</b>	<b>Objectives of the Recommended Measures &amp; Main Concern to Address</b>	<b>Who to implement the measures?</b>	<b>Location of the measure</b>	<b>When to implement the measures?</b>	<b>What requirements or standards for the measure to achieve</b>
<b>Water Quality Impact</b>						
S5.2.2.1	Construction Site Runoff Practices and measures provided in the Practice Note for Professional Persons on Construction Site Drainage, (PROPECC PN1/94) should be followed where applicable.	Control construction runoff	Contractors	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM, WPCO, EIAO
S5.2.2.2 – S5.2.2.3	<p>Sewage from Workforce</p> <ul style="list-style-type: none"><li>• Portable chemical toilets and sewage holding tanks should be provided for handling the construction sewage generated by the workforce. A licensed Contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.</li><li>• Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project. Regular environmental audit on construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site. It is anticipated that sewage generation during the construction phase of the Project would not cause water quality impact after undertaking all required measures</li></ul>	Handling of site sewage	Contractors	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM, WPCO, EIAO

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
<b>Waste Management</b>						
S6.2.2.1	<p>Good Site Practices and Waste Reduction Measures:</p> <ul style="list-style-type: none"> <li>Nomination of an approved person, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site;</li> <li>Training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling;</li> <li>Provision of sufficient waste disposal points and regular collection for disposal;</li> <li>Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;</li> <li>Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors;</li> <li>An Environmental Management Plan (EMP) should be prepared by the contractor and submitted to the Engineer for approval.</li> </ul>	Minimize waste generation during construction	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Waste Disposal Ordinance (WDO)
S6.2.3.1	<p>Waste Reduction Measures:</p> <ul style="list-style-type: none"> <li>Segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>Proper storage and site practices to minimize the potential for damage and contamination of construction materials;</li> <li>Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste;</li> <li>Sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete, metal etc.); and</li> <li>Provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling.</li> </ul>	Reduce waste generation	Contractor	Work Sites	Prior to the commencement of construction of Advance Works and Main Works of Phase 1A	WDO
S6.2.4.1 - S6.2.4.2	<p>Storage, Collection and Transportation of Waste Should any temporary storage or stockpiling of waste is required, recommendations to minimize the impacts include:</p> <ul style="list-style-type: none"> <li>Waste, such as soil, should be handled and stored well to ensure secure</li> </ul>	Minimize waste impacts arising from waste storage	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	WDO



EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
<b>Waste Management</b>						
	<ul style="list-style-type: none"> <li>containment, thus minimizing the potential of pollution;</li> <li>Stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; and</li> <li>Different locations should be designated to stockpile each material to enhance reuse.</li> <li>Remove waste in timely manner;</li> <li>Employ the trucks with cover or enclosed containers for waste transportation;</li> <li>Obtain relevant waste disposal permits from the appropriate authorities; and</li> <li>Disposal of waste should be done at licensed waste disposal facilities.</li> </ul>					
S6.2.5.2	<p>C&amp;D Materials from Site Formation</p> <ul style="list-style-type: none"> <li>Maintain temporary stockpiles and reuse excavated fill material for backfilling;</li> <li>Carry out on-site sorting;</li> <li>Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate;</li> <li>Adopt “selective demolition” technique to demolish the existing structure and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible; and</li> <li>Implement a trip-ticket system for each works contract to ensure that the disposal of C&amp;D materials are properly documented and verified.</li> </ul>	Minimize waste impacts from excavated and C&D materials	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Land (Miscellaneous Provisions) Ordinance, WDO, ETWB TCW No. 19/2005
S6.2.5.3	<p>C&amp;D Material from Buildings Demolition and New Building Construction</p> <ul style="list-style-type: none"> <li>The Contractor should recycle as much as possible of the C&amp;DM on-site. Public fill and C&amp;DM waste should be segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal. For example, concrete and masonry can be crushed and used as fill, and steel reinforcing bar can be used by scrap steel mills. Different areas of the work sites should be designated for such segregation and storage.</li> <li>The use of wooden hoardings shall not be allowed. An alternative material, such as metal, aluminium or alloy etc, could be used.</li> <li>Government has developed a charging policy for the disposal of waste to landfill at present. It will provide additional incentive to reduce the volume of generated waste and ensure proper segregation to allow</li> </ul>	Minimize waste impacts from building demolition and new building construction	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Land (Miscellaneous Provisions) Ordinance, WDO, ETWB TCW No. 19/2005

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
<b>Waste Management</b>						
	<p>reuse of the inert material on site when implemented.</p> <ul style="list-style-type: none"> <li>In order to minimize the impacts of the demolition works, the generated wastes must be cleared as quickly as possible after demolition. Therefore, the demolition and clearance works should be undertaken simultaneously. To facilitate proper segregation of inert and non-inert C&amp;D material arising from demolition works, selective demolition method should be adopted.</li> </ul>					
S6.2.5.4	<p>Chemical Waste</p> <ul style="list-style-type: none"> <li>If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producers.</li> <li>Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste contractor. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation</li> </ul>	Control the chemical waste and ensure proper storage, handling and disposal	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Waste Disposal (Chemical Waste General) Regulation, Code of Practice on the Packaging, Labelling and Storage of Chemical Waste
S6.2.5.5	<p>General Refuse</p> <ul style="list-style-type: none"> <li>General refuse should be stored in enclosed bins separately from construction and chemical wastes.</li> <li>Recycling bins should also be placed to encourage recycling.</li> <li>Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean.</li> <li>A reputable waste collector should be employed to remove general refuse on a daily basis.</li> </ul>	Minimize production of the general refuse and avoid odour, pest and litter impacts	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Waste Disposal (Chemical Waste General) Regulation, Code of Practice on the Packaging, Labelling and Storage of Chemical Waste

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
<b>Landscape and Visual</b>						
S7.3.1.1	<p>Good Site Practices</p> <ul style="list-style-type: none"> <li>For areas unavoidably disturbed by the Project on a short term basis e.g. works areas, the general principle to try and restore these to their former state to suit future land use, should be adhered to.</li> <li>With regard to topsoil, where identified, it should be stripped, treated appropriately, and where suitable and practical stored for re-use in the construction of the soft landscape works such as roadside amenity strips, and open space sites.</li> </ul>	Minimize the impact to the landscape and visual	Contractor	Work Sites	Prior to construction and construction phase	
S7.3.2.1	<p>MM4 - Tree Protection &amp; Preservation</p> <ul style="list-style-type: none"> <li>Existing trees to be retained within the Project Site should be carefully protected during construction. In particular Old and Valuable Trees (OVTs) will be preserved according to ETWB TC (Works) No. 29/2004. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in Contractor's works areas. A detailed tree survey will be carried out for the Tree Removal Application (TRA) process which will be carried out at the later detailed design stage of the Project. The detailed tree survey will propose which trees should be retained, transplanted or felled and will include details of tree protection measures for those trees to be retained.</li> </ul>	Protect and Preserve Trees	Designer / Contractor	Work Sites	Prior to construction and construction phase	ETWB TCW No. 10/2013, 29/2004 and 3/2006
S7.3.2.1	<p>MM5 - Tree Transplantation</p> <ul style="list-style-type: none"> <li>Trees unavoidably affected by the Project works should be transplanted where practical. Trees should be transplanted straight to their final receptor site and not held in a temporary nursery as far as possible. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, where applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme. A detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBTC 2/2004 and 3/2006 and final</li> </ul>	Transplant Trees where suitable for transplantation	Designer / Contractor	Work Sites where possible. Otherwise consider offsite locations	Prior to construction, construction phase and operation phase	WB TCW No. 10/2013, 3/2006 and 2/2004

**DSD Contract No: DC/2013/09**

**Advance Works for Shek Wu Hui Sewage Treatment Works – Further Expansion Phase 1A and Sewerage Works at Ping Che Road**

**4<sup>th</sup> Quarterly Environmental Monitoring and Audit (EM&A) Summary Report (July to September 2016)**

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
<b>Landscape and Visual</b>						
	locations of transplanted trees should be agreed prior to commencement of the work.					
S7.3.2.1	MM17 - Light Control <ul style="list-style-type: none"> <li>Construction day and night time lighting should be controlled to minimize glare impact to adjacent VSRs during the Construction phase. Street and night time lighting shall also be controlled to minimize glare impact to adjacent VSRs during the operation phase.</li> </ul>	To minimize glare impact to adjacent VSRs.	Designer / Contractor	Work Sites and/or the Plant	Construction phase and operation phase	
