



翠谷工程有限公司 Green Valley Landfill, Limited

# South East New Territories (SENT) Landfill Extension

**Quarterly Environmental Monitoring & Audit Report No.12** 

March 2022

ERM

2509, 25/F One Harbourfront 18 Tak Fung Street Hunghom, Kowloon Hong Kong T: 2271 3000 F: 3015 8052 www.erm.com





## South East New Territories (SENT) Landfill Extension

## Environmental Certification Sheet EP-308/2008/B and FEP-01/308/2008/B

#### **Reference Document/Plan**

Document/Plan to be Certified/Verified:	Quarterly Environmental Monitoring & Audit Report No. 12 for South East New Territories (SENT) Landfill Extension
Date of Report:	8 March 2022

#### **Reference EM&A Manual Requirement**

EM&A Manual:

Section 11.4

The quarterly EM&A summary report shall be prepared by the ET, certified by the ET Leader and verified by the IEC. The quarterly EM&A summary report should contain all information listed under Section 11.4 of the approved EM&A Manual.

#### ET Certification

I hereby certify that the above referenced document/plan complies with the above referenced EM&A Manual requirement.

Frank Wan, Environmental Team Leader: (ERM Hong-Kong, Limited)

Warchitty.

Date: 8 March 2022

#### IEC Verification

I hereby verify that the above referenced document/plan complies with the above referenced EM&A Manual requirement.

W.K. Chiu, Independent Environmental Checker:

b

Date: 10 March 2022

(Meinhardt Infrastructure and Environment Limited)

## South East New Territories (SENT) Landfill Extension

## Quarterly Environmental Monitoring & Audit Report No.12

#### Environmental Resources Management

2509, 25/F, One Harbourfront 18 Tak Fung Street Hunghom, Kowloon Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 3015 8052 E-mail: post.hk@erm.com http://www.erm.com

Client:		Projec	t No:		
Green V	alley Landfill Ltd.	0465	169		
Summary:		Date:			
		8 Ma	rch 2022		
		Appro	ved by:		
	Iment presents the Quarterly EM&A Report No.12 for st New Territories (SENT) Landfill Extension	W	nch-1	tJ.	
		Franl Partn	k Wan er		
		i arai	01		
0	Quarterly EM&A Report No.12	AL	FW	FW	8 Mar 22
Revision	Description	Ву	Checked	Approved	Date
of 'ERM Hor	has been prepared by Environmental Resources Management the trading name ng-Kong, Limited', with all reasonable skill, care and diligence within the terms act with the client, incorporating our General Terms and Conditions of Business	Distrib	oution		
	ccount of the resources devoted to it by agreement with the client.		Internal		
We disclaim scope of the	any responsibility to the client and others in respect of any matters outside the above.	$\boxtimes$	Public		
to third parti	s confidential to the client and we accept no responsibility of whatsoever nature es to whom this report, or any part thereof, is made known. Any such party report at their own risk.		Confide	ntial	
			ISO 900 Qualit Manad	gement Oc He	0 5001 cupational alth and Safety inagement



	EXECUTIVE SUMMARY	1
1	INTRODUCTION	1
1.1	BACKGROUND	1
1.2	PROJECT DESCRIPTION	1
1.3	SCOPE OF THE EM&A REPORT	2
1.4	PROJECT ORGANISATION	2
1.5	SUMMARY OF CONSTRUCTION WORKS	3
1.6	SUMMARY OF EM&A PROGRAMME REQUIREMENTS	5
1.7	STATUS OF STATUTORY ENVIRONMENTAL COMPLIANCE WITH THE	
	Environmental Permit	6
1.8	STATUS OF OTHER STATUTORY ENVIRONMENTAL REQUIREMENTS	6
2	EM&A RESULTS	8
2.1	AIR QUALITY MONITORING	8
2.2	NOISE MONITORING	17
2.3	WATER QUALITY MONITORING	20
2.4	LANDFILL GAS MONITORING	29
2.5	LANDSCAPE AND VISUAL MONITORING	33
2.6	EM&A SITE INSPECTION	34
2.7	WASTE MANAGEMENT STATUS	37
2.8	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	38
2.9	SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMAN	NCE
	LIMIT	38
2.10	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL	
	PROSECUTIONS	38
3	CONCLUSION AND RECOMMENDATION	40

ANNEXES

ANNEX A WORK PROGRAMME

ANNEX B ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE

ANNEX C MONITORING SCHEDULE FOR THIS REPORTING PERIOD

ANNEX D AIR QUALITY

ANNEX D1 24-HOUR TSP MONITORING RESULTS

ANNEX D2 EVENT AND ACTION PLAN FOR AIR QUALITY MONITORING

ANNEX D3 METEOROLOGICAL DATA

ANNEX D4 ODOUR MONITORING RESULTS

ANNEX D5 THERMAL OXIDIZER, LANDFILL GAS FLARE AND LANDFILL GAS GENERATOR STACK EMISSION MONITORING RESULTS

ANNEX D6 INVESTIGATION REPORTS OF ENVIRONMENTAL QUALITY LIMIT EXCEEDANCE

ANNEX E NOISE

ANNEX E1 NOISE MONITORING RESULTS

ANNEX E2 EVENT AND ACTION PLAN FOR NOISE MONITORING

ANNEX F WATER QUALITY

ANNEX F1 SURFACE WATER QUALITY MONITORING RESULTS

ANNEX F2 EVENT AND ACTION PLAN FOR WATER QUALITY MONITORING

ANNEX F3 LEACHATE LEVELS MONITORING RESULTS

ANNEX F4 EFFLUENT QUALITY MONITORING RESULTS

ANNEX F5 GROUNDWATER MONITORING RESULTS

ANNEX F6 INVESTIGATION REPORTS OF ENVIRONMENTAL QUALITY LIMIT EXCEEDANCE

ANNEX G LANDFILL GAS

ANNEX G1 LANDFILL GAS MONITORING LOCATIONS FOR SERVICE VOIDS, UTILITIES AND MANHOLES ALONG THE SITE BOUNDARY AND WITHIN THE SENTX SITE

ANNEX G2 LANDFILL GAS MONITORING RESULTS

ANNEX G3 EVENT AND ACTION PLAN FOR LANDFILL GAS MONITORING

ANNEX H CUMULATIVE STATISTICS ON EXCEEDANCES, ENVIRONMENTAL COMPLAINTS, NOTIFICATION OF SUMMONS AND STATUS OF PROSECUTIONS

### EXECUTIVE SUMMARY

The SENT Landfill Extension (SENTX) forms an integral part in the Strategic Plan in maintaining the continuity of landfill capacity in the Hong Kong for the cost-effective and environmentally satisfactory disposal of waste. ERM-Hong Kong, Limited (ERM) is commissioned to undertake the role of Environmental Team (ET) for the construction, operation/restoration and aftercare of SENTX Project ("the Project") in accordance with the requirements specified in the Environmental Permit (EP), updated Environmental Monitoring and Audit (EM&A) Manual, the approved Environmental Impact Assessment (EIA) Report of the Project taking account of the latest design and other relevant statutory requirements. The construction (not including works related to site clearance and preparation) of the Project commenced on 2 January 2019.

This Quarterly EM&A report presents the EM&A works carried out during the period from 1 October to 31 December 2021 for the Project in accordance with the updated EM&A Manual.

### Exceedance of Action and Limit Levels for Air Quality

One exceedance of the Limit Level for Total Suspended Particulates (TSP) and one exceedance of the Limit Level for landfill gas flare stack emission (Carbon Monoxide (CO)) were recorded for air quality impact monitoring in the reporting period. The TSP exceedance at AM4 on 13 December 2021 was considered non Project-related upon further investigation. The landfill gas flare stack emission (CO) exceedance on 17 December 2021 was found to be Project-related.

## Exceedance of Action and Limit Levels for Noise

No exceedance of Action and Limit Levels for construction and operation/ restoration phase noise monitoring was recorded in the reporting period.

## Exceedance of Action and Limit Levels for Water Quality

One exceedance of the Limit Level for groundwater (Chemical Oxygen Demand (COD)) was recorded for water quality impact monitoring in the reporting period. The groundwater (COD) exceedance at MWX-6 on 8 December 2021 was considered non Project-related upon further investigation.

## Exceedance of Action and Limit Levels for Landfill Gas

No exceedance of Action and Limit Levels for operation/ restoration phase landfill gas monitoring was recorded in the reporting period.

### **Environmental Complaints, Summons and Prosecutions**

There were no complaints, notification of summons or prosecution recorded in the reporting period.

## **Reporting Change**

There was no reporting change in the reporting period.

#### 1 INTRODUCTION

#### 1.1 BACKGROUND

The SENT Landfill Extension (SENTX) forms an integral part in the Strategic Plan in maintaining the continuity of landfill capacity in the Hong Kong for the cost-effective and environmentally satisfactory disposal of waste. The *Environmental Impact Assessment (EIA) Report* and the associated *Environmental Monitoring and Audit (EM&A) Manual* for the construction, operation, restoration and aftercare of the SENTX (hereafter referred to as "the Project") have been approved under the *Environmental Impact Assessment Ordinance (EIAO)* in May 2008 (Register No.: AEIAR-117/2008) (hereafter referred to as the approved EIA Report) and an Environmental Permit (EP-308/2008) (EP) was granted by the Director of Environmental Protection (DEP) on 5 August 2008.

Since then, applications for Variation of an Environmental Permit (No. VEP-531/2017) were submitted to EPD and the Variation of Environmental Permits (EP-308/2008/A and EP-308/2008/B) were granted on 6 January 2012 and 20 January 2017, respectively, as the Hong Kong SAR Government has decided to reduce the scale of the design scheme of SENTX assessed in the approved EIA Report and SENTX will only receive construction waste. In May 2018, a Further Environmental Permit (FEP) (FEP-01/308/2008/B) was granted to the SENTX's contractor, Green Valley Landfill, Limited (GVL).


ERM-Hong Kong, Limited (ERM) and Meinhardt Infrastructure and Environment Limited (Meinhardt) are commissioned to undertake the roles of Environmental Team (ET) and the Independent Environmental Checker (IEC), respectively, to undertake the EM&A activities for the Project in accordance with the requirements specified in the EP, updated EM&A Manual <sup>(1)</sup>, approved EIA Report <sup>(2)</sup> taking account of the latest design and other relevant statutory requirements.

#### 1.2 **PROJECT DESCRIPTION**

The SENTX is a piggyback landfill, occupying the southern part of the existing SENT Landfill (including its infrastructure area) and 13 ha of Tseung Kwan O (TKO) Area 137. A layout plan of the SENTX is shown in *Figure 1.1*. Under the latest design, the SENTX has a net void capacity of about 6.5 Mm<sup>3</sup> and provides an additional lifespan of about 6 years, commencing operation upon exhaustion of the SENT Landfill. The SENTX will receive construction waste only.

<sup>(1)</sup> ERM (2018). South East New Territories (SENT) Landfill Extension: Environmental Monitoring & Audit Manual

<sup>(2)</sup> ERM (2007). South East New Territories (SENT) Landfill Extension – Feasibility Study: Environmental Impact Assessment Report

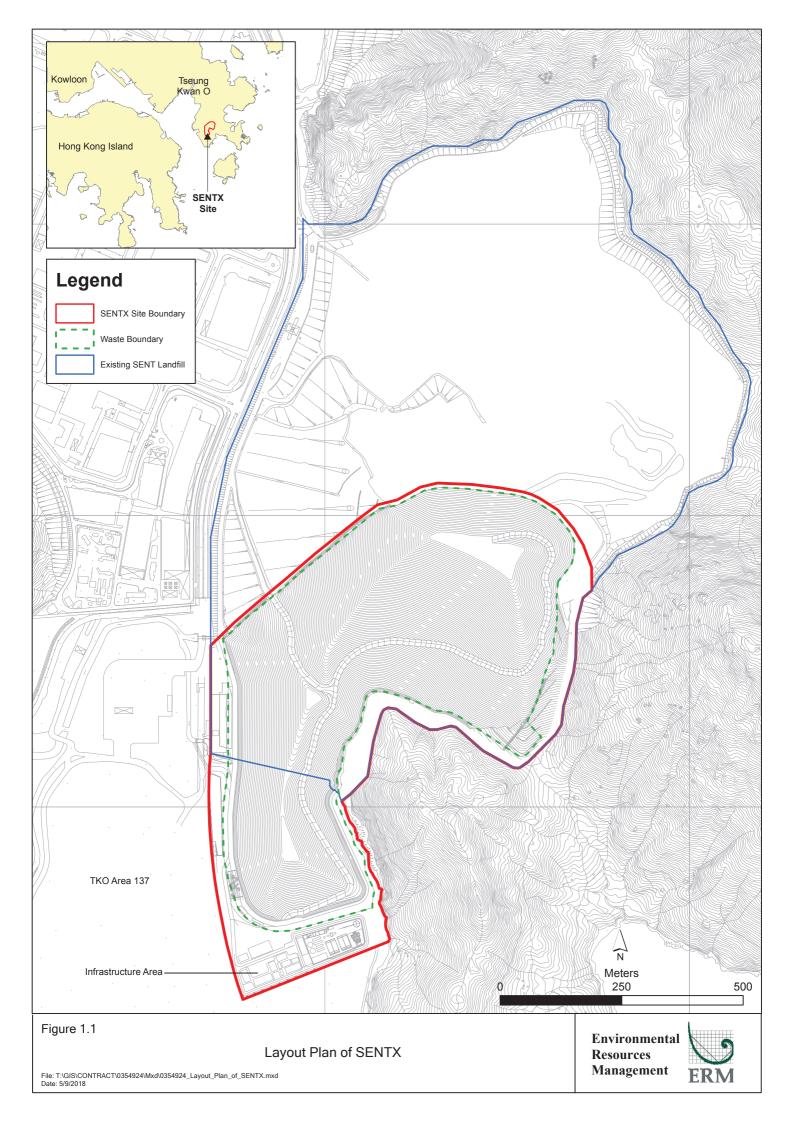

The key implementation milestones of the Project are indicatively summarised in *Table 1.1*. The construction works and operation of the Project commenced on 2 January 2019 and 21 November 2021, respectively.

## Table 1.1Estimated Key Dates of Implementation Programme

Key Stage of the Project	Indicative Date
Start construction	2 January 2019
Commissioning of new infrastructure facilities	2020
Demolition of existing infrastructure facilities	2021
Start waste intake at SENTX	21 November 2021
Estimated exhaustion date of SENTX	2027
End of aftercare for SENTX	2057

The major construction works of the SENTX includes:

- Site formation at the TKO Area 137 and the existing infrastructure area at SENT Landfill;
- Construction of surface and groundwater drainage systems;
- Construction of the leachate containment and collection systems;
- Construction of new leachate and landfill gas treatment facilities, site offices, maintenance yards at the new infrastructure area;
- Construction of new pipelines to transfer the leachate and landfill gas collected from the existing SENT Landfill to the treatment facilities at the new infrastructure area;
- Construction of the site access and new waste reception facilities; and
- Demolition of the facilities at the existing SENT Landfill infrastructure area.


### 1.3 SCOPE OF THE EM&A REPORT

This is the Quarterly EM&A Report for the Project which summarises the key findings of the EM&A programme during the reporting period from 1 October to 31 December 2021 for the construction and operation works.

### 1.4 **PROJECT ORGANISATION**

The organisation structure of the Project is presented in *Figure 1.2*.

## Figure 1.2 Organisation Chart

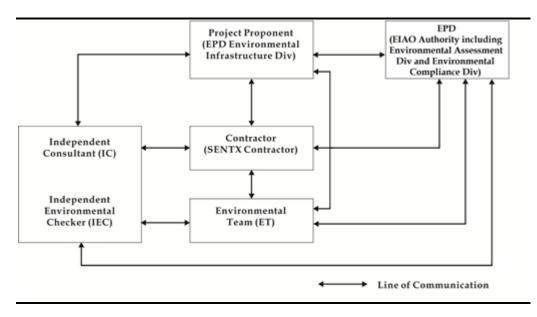

Contact details of the key personnel are summarized in *Table 1.2* below.

#### Table 1.2Contact Information of Key Personnel

Party	Position	Name	Telephone
Contractor (Green Valley Landfill	Project Manager	Gary Barnicott	2706 8827
Limited)			
Environmental Team (ET) (ERM-Hong Kong, Limited)	ET Leader	Frank Wan	2271 3152
Independent Environmental Checker (IEC) (Meinhardt Infrastructure and Environment Limited)	IEC	W.K. Chiu	2858 0738

#### 1.5 SUMMARY OF CONSTRUCTION WORKS

The programme of the construction is shown in *Annex A*. As informed by the Contractor, the major works carried out in this reporting period include:

#### October 2021

- Follow up on civil provision work detects at Landfill Gas (LFG) Plant, Leachate Treatment Plant (LTP) and infrastructure area;
- Construction of screeding at LTP;
- Permanent equipment installation for sump houses 1, 2 and 3;
- Construction of mechanically stabilised earth (MSE) wall and Cell 4X formation;
- Maintenance and improvement of temporary surface water drainage; and

• Underground utilities and pipes installation at waste reception area.

## November 2021

- Follow up on civil provision work detects at LFG Plant, LTP, infrastructure area and waste reception area;
- Construction of screeding at LTP;
- Permanent equipment installation for sump houses 1, 2 and 3;
- Maintenance and improvement of temporary surface water drainage;
- Demolition of SENT infrastructure buildings; and
- Liner works at Cell 4X.

### December 2021

- Follow up on civil provision work defects at LFG Plant, LTP, infrastructure area and waste reception area;
- Construction of MSE wall;
- Site formation for Cell 4X;
- Liner works at Cell 4X; and
- Maintenance and improvement of temporary surface water drainage.

The implementation schedule of the mitigation measures recommended in the Updated EM&A Manual is presented in *Annex B*.

#### 1.6 SUMMARY OF EM&A PROGRAMME REQUIREMENTS

The status for all environmental aspects are presented in *Table 1.3*. The EM&A requirements remained unchanged during the reporting period.

## Table 1.3Summary of Status for the Environmental Aspects under the Updated EM&A<br/>Manual

Parameters	Status
Air Quality	
Baseline Monitoring	The results of baseline air quality monitoring were reported in Baseline Monitoring Report and Pre-operation Baseline Monitoring Report and submitted to EPD under EP Condition 3.3
Impact Monitoring	On-going
Noise	
Baseline Monitoring	The results of baseline noise monitoring were reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.3
Impact Monitoring	On-going
Water Quality	
Baseline Monitoring	The results of baseline surface water quality monitoring were reported in Baseline Monitoring Report and Pre-operation Baseline Monitoring Report and submitted to EPD under EP Condition 3.3
Impact Monitoring	On-going
Landfill Gas	
Impact Monitoring	On-going
Waste Management	
Waste Monitoring	On-going
Landscape and Visual	
Baseline Monitoring	The results of baseline landscape and visual monitoring were reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.3
Construction Phase Audit	On-going
Site Environmental Audit	
Regular Site Inspection	On-going
Complaint Hotline and Email Channel	On-going
Environmental Log Book	On-going

Taking into account the construction/operation works, impact monitoring of air quality, noise, water quality, landfill gas and waste management were carried out in the reporting period. The impact monitoring schedule of air quality, noise, water quality and landfill gas monitoring are provided in *Annex C*.

The EM&A programme also involved environmental site inspections and related auditing conducted by the ET for checking the implementation of the required environmental mitigation measures recommended in the approved EIA Report and relevant EP submissions. To promote the environmental awareness and enhance the environmental performance of the contractors, environmental trainings and regular environmental management meetings were conducted during the reporting period, which are summarised as below:

• Three environmental management meetings were held with the Contractor, ER, ET, IEC and EPD on 21 October, 26 November and 16

#### December 2021; and

- Environmental toolbox trainings on the following topics were provided by the Contractor to the workers:
  - Cut Down Construction Dust on 6 October 2021;
  - Waste Water Management on 20 October 2021;
  - Trip Ticket System on 10 November 2021;
  - Illegal Dumping on 23 November 2021;
  - Noise Control Ordinance on 8 December 2021; and
  - Air Pollution Control (NRMM) Regulation on 22 December 2021 .

## 1.7 STATUS OF STATUTORY ENVIRONMENTAL COMPLIANCE WITH THE ENVIRONMENTAL PERMIT

The status of statutory environmental compliance with the EP conditions under the EIAO, submission status under the EP and implementation status of the recommended mitigation measures are presented in *Table 1.4*.

## Table 1.4Status of Submissions required under the EP and Implementation Status of<br/>the recommended Mitigation Measures

EP Condition	Submission / Implementation Status	Status
2.3	Management Organisation of Main Construction Companies	Submitted and accepted by EPD.
2.4	Setting up of Community Liaison Group	Community Liaison Group was set up.
2.5	Submission of Detailed Landfill Gas Hazard Assessment Report	Submitted, and accepted by EPD on 10 January 2019.
2.6	Submission of Restoration and Ecological Enhancement Plan	Submitted to EPD on 28 June 2019.
2.7	Setting up of Trial Nursery	Trial Nursery works was commenced on 28 August 2019.
2.8	Advance Screen Planting	Advance Screen Planting works were completed on 28 June 2019.
2.9	Provision of Multi-layer Composite Liner System	Under implementation.

### 1.8 STATUS OF OTHER STATUTORY ENVIRONMENTAL REQUIREMENTS

The environmental licenses and permits (including EP, *Water Pollution Control Ordinance* (WPCO) discharge license, registration as a chemical waste producer, and construction noise permit) that are valid in the reporting period are presented in *Table 1.5*. No non-compliance with environmental statutory requirements was identified.

Description	Ref No.	Status
Environmental Permit	EP-308/2008	Granted on 5 August 2008
Variation of Environmental Permit	EP-308/2008/A	Granted on 6 January 2012
	EP-308/2008/B	Granted on 20 January 2017
Further Environmental Permit	FEP-01/308/2008/B	Granted on 16 May 2018
Water Discharge License under WPCO (Permit Holder: Chun Wo)	Licence No.: WT00033525- 2019	Validity from 27 March 2019 to 31 March 2024
Water Discharge License under WPCO (Permit Holder: GVL)	Licence No.: WT00036269- 2020	Validity from 21 June 2020 to 30 June 2022
Billing Account for Disposal of Construction Waste	Chit Account Number: 5001692	Approved on 28 December 2005
Registration as a Chemical Waste Producer (Permit Holder: Chun Wo)	5213-839-C3507-10	Issued on 23 August 2018
Registration as a Chemical Waste Producer (Permit Holder: REC)	5518-839-R2289-06	Issued on 24 October 2019
Construction Noise Permit (Permit Holder: GVL)	GW-RE0990-21	Validity from 6 October 2021 to 5 April 2022
Construction Noise Permit (Permit Holder: Chun Wo)	GW-RE0564-21	Validity from 7 June 2021 to 6 December 2021
Construction Noise Permit (Permit Holder: Paul Y.)	GW-RE1138-21	Validity from 16 November 2021 to 15 February 2022

#### EM&A RESULTS

2

The EM&A programme for the Project required environmental monitoring for air quality, noise, water quality and landfill gas as well as environmental site inspections for air quality, noise, water quality, landfill gas, waste management, and landscape and visual impacts. The EM&A requirements and related findings for each component are summarised in the following sections.

#### 2.1 AIR QUALITY MONITORING

#### 2.1.1 Dust Monitoring

#### Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, impact air quality monitoring (dust, in term of Total Suspended Particulates (TSP)) was carried out at the two designated monitoring locations (i.e. DM1 and DM2) and four designated locations along the site boundary (i.e. AM1, AM2, AM3 and AM4) during the construction and operation/restoration phase, respectively, at a 6day interval. During the construction phase, as there are two existing TSP monitoring stations (i.e. TKO-A1 and TKO-A2a) currently operating by the Civil Engineering and Development Department (CEDD) to monitor the 24hour TSP levels at the proposed dust monitoring stations for the SENTX, it is considered that the CEDD monitoring data can represent the dust condition of the SENTX during the construction phase.

The Action and Limit Levels of the air quality monitoring is provided in *Table 2.1* below.

### Table 2.1Action and Limit Levels for 24-hour TSP

Monitoring Station	Action Level	Limit Level
Construction Phase:		
DM-1 – Site Egress of TKO Area 137 Fill Bank	204 µg m- <sup>3</sup>	260 μg m- <sup>3</sup>
DM-2A -Combined Reception and Exit Office (CREO) of	193 μg m- <sup>3</sup>	260 μg m- <sup>3</sup>
TKO Area 137 Fill Bank		
Operation/ Restoration Phase:		
AM1 - SENTX Site Boundary (North)		
AM2 - SENTX Site Boundary (West, near DP3)	2(0	2(0
AM3 - SENTX Site Boundary (West, near RC15)	260 μg m- <sup>3</sup>	260 μg m- <sup>3</sup>
AM4 - SENTX Site Boundary (West, near EPD building)		

High volume air samplers (HVSs) in compliance with the specifications listed under Section 3.2.2 of the updated EM&A Manual were used to measure 24hour TSP levels at the CEDD dust monitoring stations. The HVSs were calibrated upon installation and thereafter at bi-monthly intervals to check the validity and accuracy of the results. The equipment used in the impact air quality monitoring programme and monitoring locations are summarised in *Table 2.2* and illustrated in *Figure 2.1* respectively.

### Table 2.2Dust Monitoring Details


Monitoring Station	Location	Parameter	Frequency and Duration	Monitoring Dates	Equipment
Construction	n Phase				
DM1	Site Egress of TKO Area 137 Fill Bank	24-hour TSP	Once every 6 days	3, 11, 15, 21, 27 October 2021	HVS Greasby 105 (S/N: 9795 (ET/EA/003/18))
DM2	Combined Reception and Exit Office (CREO) of TKO Area 137 Fill Bank			2, 8, 14, 20 November 2021	HVS Andersen G1051 (S/N: 1176 (ET/EA/003/05))
Operation/ I	Restoration Phase				
AM1	SENTX Site Boundary (North)	24-hour TSP	Once every 6 days	25 November	Tisch TE-5170 (S/N: 1190)
AM2	SENTX Site Boundary (West, near DP3)			2021 1, 7, 13, 19, 25, 31	Tisch TE-5170 (S/N: 1047)
AM3	SENTX Site Boundary (West, near RC15)			December 2021	Tisch TE-5170 (S/N: 1258)
AM4	SENTX Site Boundary (West, near EPD building)				Tisch TE-5170 (S/N: 1101)

Monitoring Schedule for the Reporting Period

The schedule for air quality monitoring during the reporting period is provided in *Annex C*.

#### Results and Observations

The 24-hour TSP monitoring results are summarised in *Table 2.3*. The detailed monitoring results and the graphical presentation of the 24-hour TSP monitoring results at each monitoring location are provided in *Annex D1*.

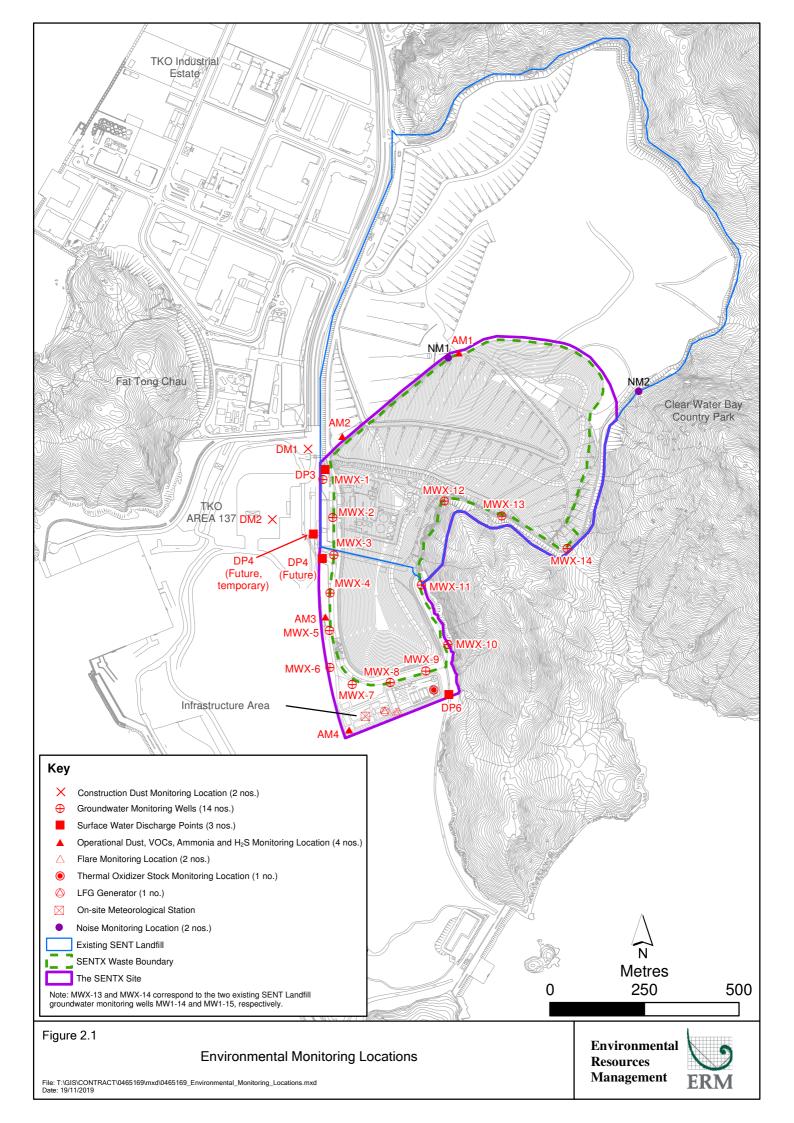

### Table 2.3Summary of 24-hour TSP Monitoring Results in the Reporting Period

Month	Monitoring	24-hr TSP Concentration (µg m <sup>-3</sup> )		Action Level	Limit Level
	Station	Average	Range	(µg/m³)	(µg/m³)
Construction Ph	ase				
October 2021	DM-1	98	92 - 112	204	260
	DM-2	92	86 - 104	193	260
November 2021	DM-1	101	94 - 109	204	260
	DM-2	91	86 - 197	193	260
Operation/ Rest	oration Phase				
November 2021	AM1	100	-	260	260
	AM2	154	-	260	260
	AM3	158	-	260	260
	AM4	235	-	260	260
December 2021	AM1	112	57 - 173	260	260
	AM2	129	100 - 156	260	260
	AM3	182	128 - 258	260	260
	AM4	168	102 - 282	260	260

The major dust sources in the reporting period included fugitive dust emission from exposed area in SENTX, as well as nearby operations of the SENT landfill and the TKO Area 137 Fill Bank.

Action and Limit Levels exceedance was recorded for TSP monitoring in the reporting period and actions in accordance with the Event and Action Plan presented in *Annex D2* were undertaken. Investigation of the Action and Limit Levels exceedance was conducted and the investigation report is presented in *Annex D6*.

Based on the investigation conducted for the monitoring event with potential Action and Limit Levels exceedance with the Contractor and the IEC, the TSP exceedance at AM4 on 13 December 2021 was considered non Project-related. The Contractor was reminded to implement all relevant mitigation measures for the construction and operation works and maintain good site practice. The ET will keep track on the monitoring data and ensure Contractor's compliance of the environmental requirements.

#### Meteorological Data

Meteorological data obtained from the SENTX on-site meteorological monitoring station was used for the dust monitoring and is shown in *Annex D3*. It is considered that meteorological data obtained at the on-site meteorological monitoring station is representative of the Project area and could be used for the construction/operation phase dust monitoring programme for the Project.

### 2.1.2 Odour Monitoring

### Monitoring Requirements

According to the updated EM&A Manual of the Project, odour patrol was carried out along the site boundary during the operation/ restoration phase. During the first month of operation, daily odour patrol (3 times per day) was conducted jointly by the ET and the IEC. The odour intensity detected was based on that determined by the IEC. In addition, an independent party (ALS Technichem (HK) Pty Ltd.) was appointed to undertake odour patrol together with the ET and IEC three times per week. During these patrols, the odour intensity detected was based on that determined by the independent third party.

The Action and Limit Levels for odour patrol is provided in *Table 2.4* below.


Table 2.4Action and Limit Levels for Odour Patrol

Perceived odour • Odour intensity $\geq$ Class 2	
intensity and odour recorded; or complaints One documented complaint received	<ul> <li>Odour intensity ≥ Class 3 recorded on 2 consecutive patrol <sup>(a) (b)</sup></li> </ul>

(b) The exceedances of the odour intensity do not need to be recorded at the same location.

Odour patrol was conducted by trained personnel / competent persons with a specific sensitivity to a reference odour (i.e. on reference materials n-butanol with the concentration of 50ppm in nitrogen (v/v)) in compliance with Section 3.7.2 of the updated EM&A Manual patrolling and sniffing along the SENTX Site boundary to detect any odour.

The odour monitoring programme and patrol route are summarised in *Table* 2.5 and illustrated in *Figure* 2.2 respectively.

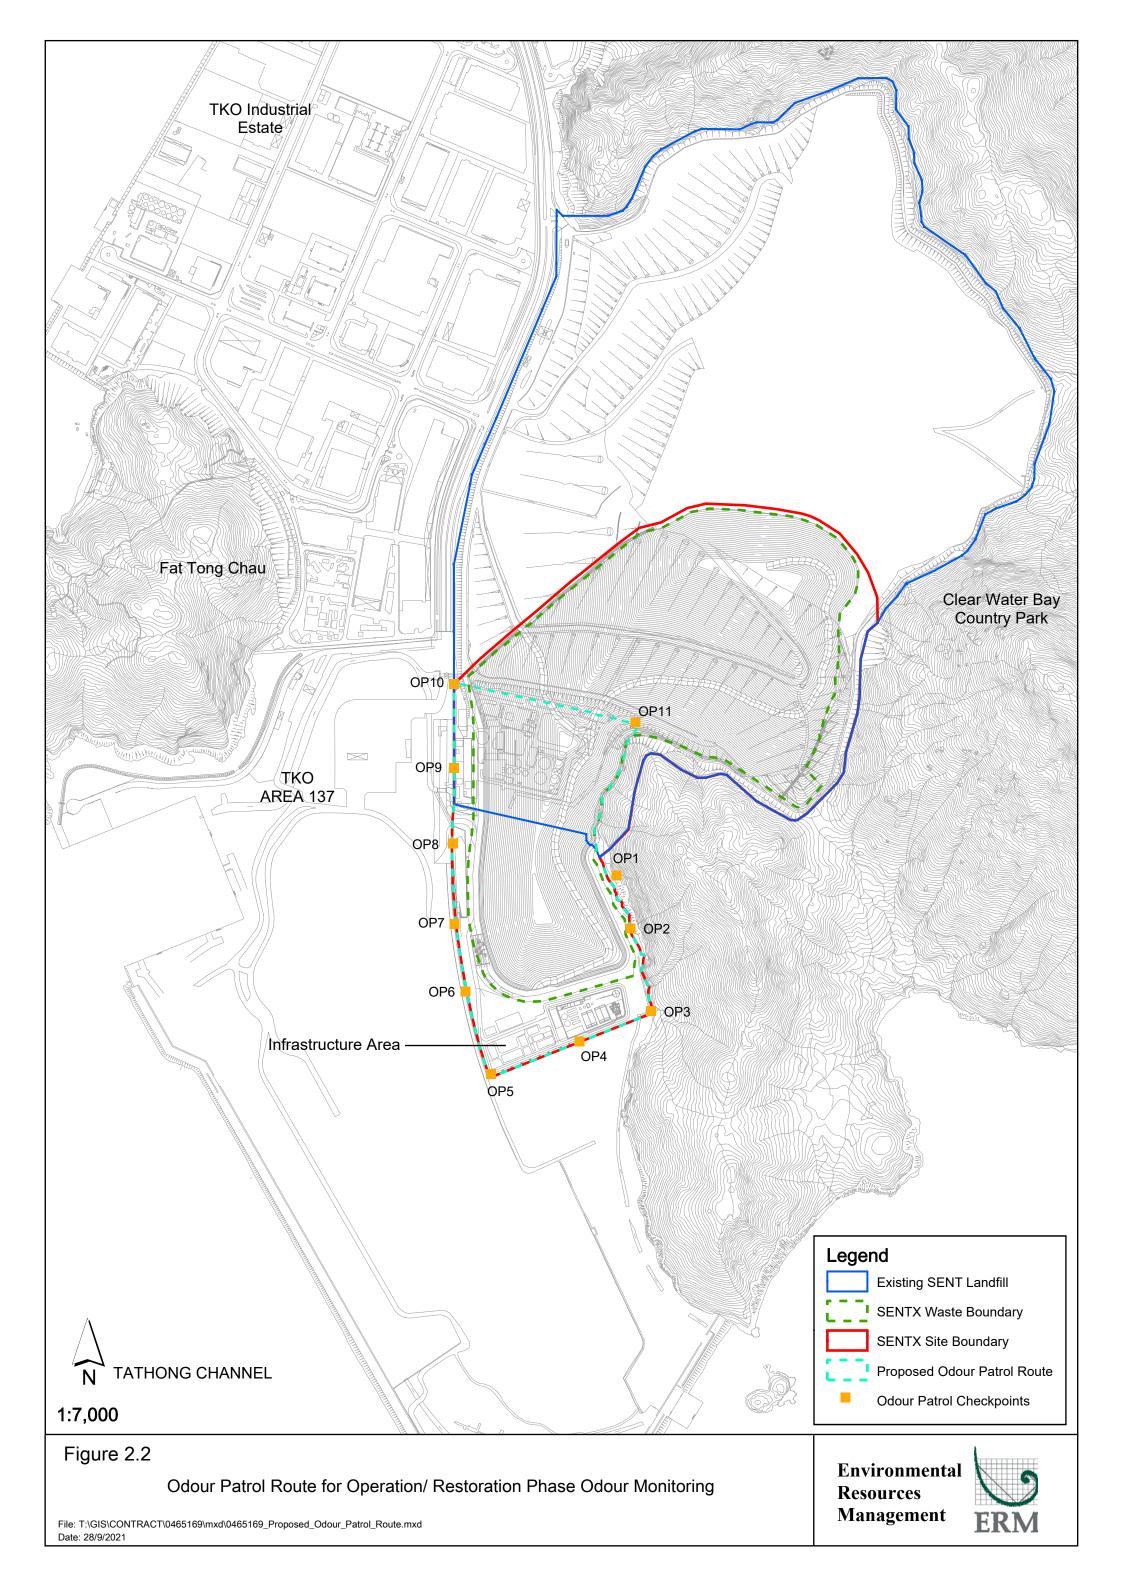

Parameters	Patrol Frequency (a)	Monitoring Dates and
		Time
Odour Intensity (see	<u>Period 1 - First month of operation</u> Daily, three times a day in the morning,	Conducted by ET & IEC:
		21 – 30 Nov 2021,
,		1 – 31 Dec 2021
	ET and the IEC	(10:30 - 12:00, 14:30 -
		16:00, 18:00 - 19:30)
	Three times per week on different days	,
	conducted by an independent third	Conducted by an
	party together with the ET and IEC <sup>(b)</sup>	independent third
		party, ET & IEC:
	Period 2 - Three months following	22 Nov 2021 (14:30 -
	period 1 (c)	16:00), 24 Nov 2021
		(10:00 - 12:00), 26 Nov
	Weekly conducted by the ET and the	2021 (14:30 - 16:00), 29
	IEC	Nov 2021 (14:30 -
		16:00), 1 Dec 2021
	Once every two weeks conducted by an	(14:30 - 16:00), 3 Dec
	independent third party together with	2021 (10:00 - 12:00), 6
	the ET and IEC (b)	Dec 2021 (14:30 -
		16:00), 8 Dec 2021
	Period 3 - Throughout operation	(10:00 – 12:00), 10 Dec
	0.1	2021 (10:00 - 12:00), 13
		Dec 2021 (10:00 -
	IEC	12:00), 15 Dec 2021
		(10:00 – 12:00), 17 Dec
		2021 (14:30 - 16:00), 20
		Dec 2021 (10:00 -
	IEC (b)	12:00), 22 Dec 2021
		(14:30 <b>-</b> 16:00), 24 Dec
		2021 (14:30 - 16:00), 28
		Dec 2021 (14:30 -
		16:00), 29 Dec 2021
		(10:00 – 12:00), 31 Dec
		2021 (14:30 - 16:00)
	Odour	Odour Intensity (see Table 2.6)Period 1 - First month of operation Daily, three times a day in the morning, afternoon and evening/night (between 18:00 and 22:00 hrs) conducted by the ET and the IECThree times per week on different days conducted by an independent third party together with the ET and IEC (b)Period 2 - Three months following period 1 (c)Weekly conducted by the ET and the 

#### Notes:

(a) Reduction of monitoring frequency will be subject to the monitoring results to demonstrate environmentally acceptable performance.

(b) Patrol shall be scheduled so that they are carried out together with the patrols to be carried out jointly by the ET and the IEC.

(c) Commencement of each period will be justified by the ET Leader and verified by the IEC and will be subject to agreement with the EPD (EIAO Authority) and Project Proponent.

(d) The revised odour patrol route with the addition of checkpoint OP11 was applied from 10 December 2021.

### Table 2.6Odour Intensity Level

Class	Odour Intensity	Description
0	Not Detected	No odour perceived or an odour so weak that it cannot be easily characterised or described.
1	Slight	Identified odour, slight
2	Moderate	Identified odour, moderate
3	Strong	Identified odour, strong
4	Extreme	Severe odour

The schedule for odour patrol during the reporting period is provided in *Annex C*.

Results and Observations

The odour monitoring results are summarised and provided in *Table 2.7* and *Annex D4*, respectively.

Table 2.7	Summary of Od	our Monitorino	Results in the I	Reporting Period
1 1010 2.7	Summary Of Ou		Results in the I	<i>Cporting</i> 1 <i>criou</i>

Odour Checkpoints	Odour Intensity Class (Range)	Action Level	Limit Level
OP1	0 - 1	Odour intensity $\geq$	Odour intensity $\geq$
OP2	0 - 1	Class 2 recorded	Class 3 recorded
OP3	0 - 1		on 2 consecutive patrol
OP4	0 - 1		partor
OP5	0 - 1		
OP6	0 - 1		
OP7	0 - 1		
OP8	0 - 1		
OP9	0 - 1		
OP10	0		
OP11	0 - 1		

The potential odour sources in the reporting period included the construction works, operation of leachate treatment plant, generator, slurry truck, excavator, vehicles and vegetation at SENTX, as well as nearby operations of the Town Gas Plant.

All the odour monitoring results were below the Action and Limit Levels in the reporting period. No action is thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex D2*.

## 2.1.3 Thermal Oxidiser, Landfill Gas Flare and Landfill Gas Generator Stack Emission Monitoring

Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, the performance of the thermal oxidiser, landfill gas flare and landfill gas generator was monitored when they are in operation. Gas samples were collected from the stack of the thermal oxidizer, landfill gas flare and landfill gas generator for laboratory analysis for NO<sub>2</sub>, CO, SO<sub>2</sub>, Benzene and Vinyl chloride and in-situ analysis for exhaust gas velocity at monthly interval. The operating conditions of the thermal oxidiser, landfill gas flare and landfill gas generator were also monitored continuously.

The Limit Levels for stack emission of the thermal oxidiser, landfill gas flare and landfill gas generator are provided in *Tables 2.8 – 2.10* below.

## Table 2.8Limit Levels for Stack Emission of the Thermal Oxidiser

Parameters	Limit Level	
NO <sub>2</sub>	1.58 gs <sup>-1</sup>	
СО	0.53 gs <sup>-1</sup>	
SO <sub>2</sub>	0.07 gs <sup>-1</sup>	
Benzene	3.01 x 10 <sup>-2</sup> gs <sup>-1</sup>	
Vinyl chloride	2.23 x 10 <sup>-3</sup> gs <sup>-1</sup>	
Gas combustion temperature	850°C (minimum)	
Exhaust gas exit temperature	443K (minimum) <sup>(a)</sup>	
Exhaust gas velocity	7.5 ms <sup>-1</sup> (minimum) <sup>(a)</sup>	
Note:		
(a) Level under full load condition.		

Table 2.9Limit Levels for Stack Emission of the Landfill Gas Flare

NO <sub>2</sub> CO	0.97 gs <sup>-1</sup> 2.43 gs <sup>-1</sup>
СО	$2.43 \text{ gs}^{-1}$
	2.10 80
SO <sub>2</sub>	0.22 gs <sup>-1</sup>
Benzene	4.14 x 10 <sup>-4</sup> gs <sup>-1</sup>
Vinyl Chloride	2.60 x 10 <sup>-4</sup> gs <sup>-1</sup>
Gas combustion temperature	815°C (minimum)
Exhaust gas exit temperature	923 K (minimum) <sup>(a)</sup>
Exhaust gas velocity	9.0 m s <sup>-1</sup> (minimum) <sup>(a)</sup>

Table 2.10Limit Levels for Stack Emission of the Landfill Gas Generator

Parameters	Limit Level
NO <sub>2</sub>	1.91 gs <sup>-1</sup>
СО	2.48 gs <sup>-1</sup>
SO <sub>2</sub>	0.528 gs <sup>-1</sup>
Benzene	2.47 x 10 <sup>-4</sup> gs <sup>-1</sup>
Vinyl chloride	1.88 x 10 <sup>-5</sup> gs <sup>-1</sup>
Gas combustion temperature	450°C (minimum)
Exhaust gas exit temperature	723K (minimum) <sup>(a)</sup>
Exhaust gas velocity	30.0 ms <sup>-1</sup> (minimum) <sup>(a)</sup>
Note:	
(a) Level under full load condition.	

Gas samples were collected from the centroid of the stack with stainless steel sampling probe, into inert sample containers (i.e. Canister and Tedlar Bag) and transferred to ALS Technichem (HK) Pty Ltd. (HOKLAS Registration No. 066) laboratory within 24 hours of collection for direct analysis on a gas chromatography within 48 hours after collection. The flue gas velocity of the gas stream at the exhaust of thermal oxidize was determined by S-Pitot tube during the emission sampling.

The stack emission monitoring programme and monitoring locations are summarised in *Table 2.11* and illustrated in *Figure 2.1*, respectively.

## Table 2.11Thermal Oxidiser, Landfill Gas Flare and Landfill Gas Generator Stack<br/>Emission Monitoring Details

Monitoring Location	Parameter	Frequency	Monitoring Date
Stack of Thermal Oxidiser	Laboratory analysis for NO <sub>2</sub> CO SO <sub>2</sub> Benzene Vinyl chloride In-situ analysis for Exhaust gas velocity	Monthly for the first 12 months of operation and thereafter at quarterly intervals	20 Dec 2021
	<ul> <li>Gas combustion temperature</li> <li>Exhaust temperature</li> <li>Exhaust gas velocity <sup>(a)</sup></li> </ul>	Continuously	1 - 31 Dec 2021
Stack of Landfill Gas Flare	Laboratory analysis for • NO <sub>2</sub> • CO • SO <sub>2</sub> • Benzene • Vinyl chloride In-situ analysis for • Exhaust gas velocity	Monthly for the first 12 months of operation and thereafter at quarterly intervals	17 Dec 2021
	<ul> <li>Gas combustion temperature</li> <li>Exhaust temperature</li> <li>Exhaust gas velocity <sup>(a)</sup></li> </ul>	Continuously	1 – 31 Dec 2021
Stack of Landfill Gas Generator	Laboratory analysis for • NO <sub>2</sub> • CO • SO <sub>2</sub> • Benzene • Vinyl chloride In-situ analysis for • Exhaust gas velocity	Monthly for the first 12 months of operation and thereafter at quarterly intervals	17 Dec 2021
	<ul> <li>Exhaust temperature</li> <li>Exhaust gas velocity <sup>(a)</sup></li> </ul>	Continuously	1 – 31 Dec 2021

#### Note:

(a) The exhaust gas velocity will be calculated based on the cross-section area of the stack and continuous monitored gas flow and combustion temperature data.

#### Monitoring Schedule for the Reporting Month

The schedule for thermal oxidizer, landfill gas flare and landfill gas generator stack emission monitoring during the reporting period is provided in *Annex C*.

#### **Results and Observations**

The thermal oxidizer, landfill gas flare and landfill gas generator stack emission monitoring results and detailed continuous monitoring results are summarised in *Tables* 2.12 - 2.14 and provided in *Annex D5*, respectively.

## Table 2.12Summary of Thermal Oxidiser Stack Emission Monitoring in the Reporting<br/>Period

Parameters	Monitoring Results (Range in Bracket)	Limit Level
NO <sub>2</sub>	0.38 gs <sup>-1</sup>	1.58 gs <sup>-1</sup>
СО	<0.02 gs <sup>-1</sup>	0.53 gs <sup>-1</sup>
SO <sub>2</sub>	<0.01 gs <sup>-1</sup>	0.07 gs <sup>-1</sup>
Benzene	<2 x 10 <sup>-5</sup> gs <sup>-1</sup>	3.01 x 10 <sup>-2</sup> gs <sup>-1</sup>
Vinyl chloride	<2 x 10 <sup>-5</sup> gs <sup>-1</sup>	2.23 x 10 <sup>-3</sup> gs <sup>-1</sup>
Gas combustion temperature	943°C (932°C - 984°C)	850°C (minimum)
Exhaust gas exit temperature	1,237K (1,219K <b>-</b> 1,316K)	443K (minimum) <sup>(a)</sup>
Exhaust gas velocity	15.3 <sup>(b)</sup>	7.5 ms <sup>-1</sup> (minimum) <sup>(a)</sup>

#### Note:

(a) Level under full load condition.

(b) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring. The limit level was not applicable as the stack was not operated under full load condition.

## Table 2.13Summary of Landfill Gas Flare Stack Emission Monitoring in the Reporting<br/>Period

Parameters	Monitoring Results (Range in Bracket)	Limit Level
NO <sub>2</sub>	<0.02 gs <sup>-1</sup>	0.97 gs <sup>-1</sup>
СО	2.81 gs <sup>-1</sup>	2.43 gs <sup>-1</sup>
SO <sub>2</sub>	0.11 gs <sup>-1</sup>	0.22 gs <sup>-1</sup>
Benzene	9.9 x 10 <sup>-5</sup> gs <sup>-1</sup>	4.14 x 10 <sup>-4</sup> gs <sup>-1</sup>
Vinyl chloride	<1.4 x 10 <sup>-5</sup> gs <sup>-1</sup>	2.60 x 10 <sup>-4</sup> gs <sup>-1</sup>
Gas combustion temperature	Flare 1: 864°C (820°C - 935°C)	815°C (minimum)
	Flare 2: 853°C (820°C - 894°C)	
Exhaust gas exit temperature	Flare 1: 1,059K (1,025K – 1,115K)	923 K (minimum) <sup>(a)</sup>
	Flare 2: 1,027K (944K – 1,097K)	
Exhaust gas velocity	9.1 <sup>(b)</sup>	9.0 m s <sup>-1</sup> (minimum) <sup>(a)</sup>

#### Note:

(a) Level under full load condition.

(b) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring. The limit level was not applicable as the stack was not operated under full load condition.

## Table 2.14Summary of Landfill Gas Generator Stack Emission Monitoring in the<br/>Reporting Period

Parameters	Monitoring Results (Range in Bracket)	Limit Level
NO <sub>2</sub>	0.007 gs <sup>-1</sup>	1.91 gs <sup>-1</sup>
СО	0.046 gs <sup>-1</sup>	2.48 gs <sup>-1</sup>
SO <sub>2</sub>	0.074 gs <sup>-1</sup>	0.528 gs <sup>-1</sup>
Benzene	4 x 10-6 gs-1	2.47 x 10 <sup>-4</sup> gs <sup>-1</sup>
Vinyl chloride	<1.2 x 10 <sup>-6</sup> gs <sup>-1</sup>	1.88 x 10 <sup>-5</sup> gs <sup>-1</sup>
Exhaust gas exit temperature	838K (748K - 847K)	723K (minimum) <sup>(a)</sup>
Exhaust gas velocity	17.6 (b)	30.0 ms <sup>-1</sup> (minimum) <sup>(a)</sup>

Note:

(a) Level under full load condition.

(b) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring. The limit level was not applicable as the stack was not operated under full load condition.

Limit Levels exceedance was recorded for landfill gas flare stack emission (CO) in the reporting period and actions in accordance with the Event and Action Plan presented in *Annex D2* were undertaken. Investigation of the Limit Levels exceedance was conducted and the investigation report is presented in *Annex D6*.

Based on the investigation conducted for the monitoring event with potential Limit Levels exceedance with the Contractor and the IEC, the landfill gas flare stack emission (CO) exceedance on 17 December 2021 was found to be Project-related. The Contractor was reminded to implement all relevant mitigation measures for the construction and operation works and maintain good site practice. The ET will keep track on the monitoring data and ensure Contractor's compliance of the environmental requirements.

## 2.2 NOISE MONITORING

### 2.2.1 Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, impact noise monitoring was conducted weekly at the monitoring location (i.e. NM1) to obtain one set of 30 minutes measurement between 07:00 and 19:00 hours on normal weekdays.

The Action and Limit Levels for construction and operational noise of the Project are provided in *Table 2.15* below.

Tim	e Period	Action Level <sup>(a)</sup>	Limit Level <sup>(b)</sup>
Con	struction Noise:		
	) – 19:00 hrs on nal weekdays	When one documented complaint is received from any one of the noise sensitive receivers (NSRs)	75 dB(A) at NSRs
		or	
_		75 dB(A) recorded at the monitoring station	
Ope	rational Noise:		
07:00 days	) – 19:00 hrs on all 3	When one documented complaint is received from any one of the noise sensitive	65 dB(A) at NSRs <sup>(c)</sup>
19:00 days	0 – 23:00 hrs on all s	receivers (NSRs) or 75 dB(A) recorded at the	65 dB(A) at NSRs <sup>(c)</sup>
23:00 days	0 – 07:00 hrs on all s	monitoring station	55 dB(A) at NSRs <sup>(c)</sup>
Note			
(a)			
(b)	Level. Limits specified in the GW-TM and IND-TM for construction and operational noise, respectively.		
(c)	Limit Level only apply to operational noise without road traffic and construction activities noise.		

Noise monitoring was performed by ALS Technichem (HK) Pty Ltd (HOKLAS Registration No. 066) using a sound level meter placed at the designated monitoring station NM1 (see *Figure 2.1*) in accordance with the requirements stipulated in the updated EM&A Manual. Acoustic calibrator was deployed to check the sound level meter at a known sound pressure level. Details of the deployed equipment are provided in *Table 2.16*.

Monitoring Station <sup>(1)</sup>	Location	Parameter	Frequency and Duration	Monitoring Dates	Equipment
NM1	SENTX Site	L <sub>eq (30 min)</sub>	Once per week	7, 15, 21, 28	Sound Level
	Boundary	measurement	for 30 mins	October 2021	Meter:
	(North)	between 07:00	during the		B&K 2238 (S/N:
		and 19:00	construction	4, 11, 18, 25	2285721)
		hours on	and operation	November 2021	
		normal	period of the		Rion NL-31
		weekdays	Project	2, 9, 14, 22, 28	(S/N: 00410221)
		(Monday to		December 2021	
		Saturday)			B&K 2238 (S/N:
					2285722)
					Rion NL-52
					(S/N: 00921191)
					Acoustic
					Calibrator:
					Rion NC-73
					(S/N: 10655561)
					Rion NC-74
					(S/N: 34657230)
					Rion NC-75
					(S/N: 34680623)

#### Table 2.16Noise Monitoring Details

#### 2.2.2 Monitoring Schedule for the Reporting Period

The schedule for noise monitoring during the reporting period is provided in *Annex C*.

#### 2.2.3 *Results and Observations*

A total of 13 impact noise monitoring events were scheduled during the reporting period. However, noise monitoring on 15 October 2021 was cancelled due to adverse weather. The noise monitoring results are summarised in *Table 2.17* and graphically presented in *Annex E1*.

## Table 2.17Summary of Construction/Operation Noise Monitoring Results in the<br/>Reporting Period

Month	Monitoring	Measured Noise Level L <sub>eq (30 min)</sub> , dB(A)			
	Station	Average	Range	Action and Limit Level	
October 2021	NM1	53.5	49.7 - 56.4	75	
November 2021	NM1	51.4	49.0 - 53.4	75	
December 2021	NM1	49.9	47.0 - 51.1	75	

Major noise sources identified during the noise monitoring included noise from operations of the existing SENT landfill and the TKO Area 137 Fill Bank, aircrafts and insects.

No exceedance of the Action and Limit Levels for construction/operation noise monitoring was recorded in the reporting period. No further mitigation measure was required in accordance with the Event and Action Plan presented in *Annex E2*.

#### 2.3 WATER QUALITY MONITORING

#### 2.3.1 Surface Water Quality Monitoring

#### Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, impact surface water quality monitoring were carried out at the three designated surface water discharge points (i.e. DP3, DP4 and DP6) at weekly and monthly intervals during construction phase and operation/ restoration phase, respectively to ensure that the SENTX will not cause adverse water quality impact. Temporary relocation of surface water discharge point DP4 to DP4 (Future, temporary) as an interim arrangement due to site constraints and construction sequence was approved by EPD on 14 May 2019. Impact surface water quality monitoring was carried out at DP4 (Future, temporary) (i.e. DP4T) from the monitoring event on 16 May 2019. In addition, suspension of impact surface water quality monitoring at DP3 was approved under the Baseline Monitoring Report by EPD on 24 July 2019 until the actual commencement of construction works affecting DP3 in 2022.

Dissolved Oxygen (DO) and pH value were measured *in situ* whereas the level of suspended solids (SS) were determined by ALS Technichem (HK) Pty Ltd (HOKLAS Registration No. 066).

The Action and Limit Levels of the surface water quality impact monitoring are provided in *Table 2.18*.

Parameters	Action Level	Limit Level	
	DP4 & DP6		
Construction Phase:			
DO	< 5.80 mg/L	< 5.42 mg/L	
SS	> 11.7 mg/L	>12.7 mg/L	
pН	> 8.39	> 8.40	
<b>Operation</b> / Restoration	Phase:		
Ammoniacal-nitrogen		>7.1 mg/L	
COD		> 30 mg/L	
SS		> 20 mg/L	

### Table 2.18Action and Limit Levels for Surface Water Quality

The locations of the monitoring stations for the Project are shown in *Figure 2.1*. All *in situ* monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or other international accreditation scheme before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the surface water quality monitoring programme.

Calibration for a DO meter was carried out before measurement according to the instruction manual of the equipment model. Details of the equipment used in the impact surface water quality monitoring works are provided in *Table 2.19*.

Monitoring Station	Location	Frequency	Monitoring Dates	Parameter	Equipment
Construction	n Phase:				
DP4 (Future, temporary)	Surface water discharge point DP4	Weekly	7, 15, 21, 28 October 2021 4, 11, 18 November	•pH •DO •SS	YSI Professiona DSS (S/N: 15H103928)
DP6	Surface water discharge point DP6		2021		
Operation/ I	Restoration	Phase:			
DP4 (Future, temporary) DP6	Surface water discharge point DP4 Surface water discharge point DP6	Monthly	25 November 2021, 28 December 2021	<ul> <li>Electrical</li> <li>Conductivity</li> <li>Societation</li> <li>DO</li> <li>DO</li> <li>Calleration</li> <li>SS</li> <li>Mai</li> <li>COD</li> <li>Nitrate-</li> <li>Nitrate-</li> <li>Nitrate-</li> <li>Nitrate-</li> <li>Nitrate-</li> <li>Nitrate-</li> <li>Iroo</li> </ul>	n nc prcury

#### Table 2.19Impact Surface Water Quality Monitoring Details

Notes:

- (a) DP4 was temporary relocated to DP4 (Future, temporary) (i.e. DP4T) as an interim discharge point from the monitoring event on 16 May 2019.
- (b) Impact surface water quality monitoring at DP3 was suspended from the monitoring event on 25 July 2019 until the actual commencement of construction works affecting DP3 in 2021.

#### Monitoring Schedule for the Reporting Period

The schedule for surface water quality monitoring during the reporting period is provided in *Annex C*.

#### **Results and Observations**

A total of 9 monitoring events for impact surface water quality monitoring were scheduled at all designated monitoring stations during the reporting period. However, sampling could not be carried out at the monitoring events below due to insufficient flow:

- October 2021 at all monitoring locations;
- 4 November 2021 at all monitoring locations;
- 18 November 2021 at all monitoring locations;
- 25 November 2021 at all monitoring locations; and
- 28 December 2021 at all monitoring locations.

Impact surface water quality monitoring results and graphical presentations are provided in *Annex F1*.

All the surface water monitoring results were below the Action and Limit Levels in the reporting period. No action is thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex F2*.

### 2.3.2 Leachate Monitoring

#### Monitoring Requirements and Equipment

According to the updated EM&A Manual, continuous monitoring of leachate level and daily monitoring of effluent quality were carried out during the operation/ restoration phase.

Temperature, pH and volume of the effluent discharged from the leachate treatment plant were measured in-situ whereas the parameters as listed in *Table 2.21* were determined by ALS Technichem (HK) Pty Ltd. (HOKLAS Registration No. 066).

The Limit Levels of the leachate monitoring are provided in *Table 2.20*.

### Table 2.20Limit Levels for Leachate Levels and Effluent Quality

Parameters	Limit Level
Leachate Levels	
Leachate levels above the basal liner	1 m above the primary liner of the leachate containment system
Effluent Quality	
Temperature	> 43 °C
pH Value	6 – 10
Volume Discharged	>1,500 m <sup>3</sup>
Suspended Solids (SS)	> 800 mg/L
Ammoniacal-nitrogen	> 100 mg/L
Nitrite-nitrogen	> 100 mg/L

ENVIRONMENTAL RESOURCES MANAGEMENT

Parameters	Limit Level
Phosphate	> 25 mg/L
Sulphate	> 900 mg/L
Nitrate-nitrogen	> 100 mg/L
Biochemical Oxygen Demand (BOD)	> 800 mg/L
Chemical Oxygen Demand (COD)	> 2,000 mg/L
Oil & Grease	> 20 mg/L
Boron	> 7,000 µg/L
Iron	> 7.5 mg/L
Cadmium	>1 µg/L
Chromium	> 400 µg/L
Copper	> 1,000 µg/L
Nickel	> 800 µg/L
Zinc	> 800 µg/L

All *in situ* monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or other international accreditation scheme before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the leachate quality monitoring programme. Details of the equipment used are provided in *Table 2.21*.

Location	Frequency	Parameter	Monitoring Dates	Equipment
Leachate levels above the basal liner		Leachate Levels	21 - 30 November 2021, 1 - 31 December 2021	transducers
Effluent discharged from LTP	Daily for the first 3 months upon full operation of the LTP at wet season (Apr to Sep) and dry season (Oct to Mar), respectively and reduce to monthly thereafter subject to the monitoring results of the first 3 months for each season and agreement with the EIAO Authority, IEC and IC. (a)	<ul> <li>On-site</li> <li>Measurements:</li> <li>Volume</li> <li>pH</li> <li>Temperature</li> <li>Laboratory analysis:</li> <li>Suspended Solids</li> <li>COD</li> <li>BOD<sub>5</sub></li> <li>TOC</li> <li>Ammoniacal- nitrogen</li> <li>Nitrate-nitrogen</li> <li>Nitrite-nitrogen</li> <li>Nitrite-nitrogen</li> <li>Sulphate</li> <li>Phosphate</li> <li>Oil &amp; Grease</li> <li>Alkalinity</li> <li>Chloride</li> <li>Calcium</li> </ul>	21 - 30 November 2021, 1 - 31 December 2021	Lutron WA 2017SD (S/N: T.016811)

#### *Table* 2.21 Leachate Levels and Effluent Quality Monitoring Details

Note:

(a) Reduction of monitoring frequency will be subject to the monitoring results to demonstrate environmentally acceptable performance.

 Potassium Magnesium

Iron •

Zinc •

Copper

Nickel

Boron ٠

Chromium

Cadmium

•

٠

•

٠

•

Monitoring Schedule for the Reporting Month

The schedule for leachate monitoring during the reporting period is provided in Annex C.

### **Results and Observations**

The leachate levels and effluent quality monitoring results are summarised in Table 2.22 and Table 2.23, respectively. The detailed monitoring results are provided in Annex F3 and Annex F4, respectively.

Month	Monitoring Location	Average Leachate Head Levels (cm) (Range in Bracket)	Limit Level (cm)
	Pump Station No. 1X (Cell 1X)		
November	Meter No. X-1	61 (44 - 79)	> 178
2021	Meter No. X-2	81 (64 - 99)	
	Average	71 (54 - 89)	
December	Meter No. X-1	65 (44 - 111)	
2021	Meter No. X-2	78 (10 – 111)	
	Average	71 (48 - 101)	
	Pump Station No. 2X (Cell 2X)		
December	Meter No. X-1	81 (70 - 88)	> 180
2021	Meter No. X-2	82 (73 - 88)	
	Average	81 (72 - 87)	
	Pump Station No. 3X (Cell 3X)		
December	Meter No. X-1	89 (79 – 99)	> 175
2021	Meter No. X-2	89 (79 – 99)	
	Average	89 (79 – 89)	

## Table 2.22Summary of Leachate Levels in the Reporting Period

## Table 2.23Summary of Effluent Quality Monitoring Results in the Reporting Period

Month	Parameters	Average Monitoring Results (Range in Bracket)	Limit Level
	Effluent Discharged fro		
November 2021	Temperature	25.0°C (18.6°C - 28.9°C)	> 43 °C
	pH Value	8.4 (8.3 - 8.5)	6 – 10
	Volume Discharged	981m³ (301m³ - 1,462m³)	>1,500 m <sup>3</sup>
	Suspended Solids (SS)	27.0mg/L (20.4mg/L - 35.2mg/L)	> 800 mg/L
	Ammoniacal-nitrogen	0.40mg/L (0.28mg/L – 0.84mg/L)	>100 mg/I
	Nitrite-nitrogen	0.20mg/L (0.04mg/L – 0.63mg/L)	>100 mg/I
	Phosphate	9.7mg/L (9.2mg/L – 10.3mg/L)	> 25 mg/L
	Sulphate	64mg/L (58mg/L - 70mg/L)	> 900 mg/I
	Nitrate-nitrogen	60.8mg/L (46.4mg/L – 69.6mg/L)	> 100 mg/I
	BOD	10mg/L (6mg/L - 14mg/L)	> 800 mg/I
	COD	1,018mg/L (888mg/L – 1,620mg/L)	> 2,000 mg/L
	Oil & Grease	<5mg/L (<5mg/L - <5mg/L)	> 20 mg/L
	Boron	5,246μg/L (4,900μg/L – 5,500μg/L)	> 7,000 µg/
	Iron	1.40mg/L (1.28mg/L – 1.56mg/L)	> 7.5 mg/L
	Cadmium	<1.0µg/L (<1.0µg/L - <1.0µg/L)	>1 µg/L
	Chromium	126μg/L (120μg/L – 134μg/L)	> 400 µg/L
	Copper	11μg/L (11μg/L – 11μg/L)	> 1,000 µg/
	Nickel	114μg/L (110μg/L – 117μg/L)	> 800 µg/L
	Zinc	65μg/L (60μg/L – 70μg/L)	> 800 µg/L
December 2021	Temperature	25.7°C (20.0°C – 30.6°C)	> 43 °C
	pH Value	8.4 (8.3 - 8.5)	6 - 10
	Volume Discharged	1,025m³ (473m³ - 1,435m³)	>1,500 m <sup>3</sup>
	Suspended Solids (SS)	20.0mg/L (10.1mg/L - 33.8mg/L)	> 800 mg/I

Month	Parameters	Average Monitoring Results (Range in Bracket)	Limit Level
	Ammoniacal-nitrogen	0.34mg/L (0.15mg/L – 0.75mg/L)	>100 mg/L
	Nitrite-nitrogen	0.24mg/L (0.14mg/L – 0.70mg/L)	> 100 mg/L
	Phosphate	10.0mg/L (7.7mg/L – 11.5mg/L)	> 25 mg/L
	Sulphate	68mg/L (57mg/L – 92mg/L)	>900 mg/L
	Nitrate-nitrogen	62.0mg/L (42.4mg/L – 80.3mg/L)	>100 mg/L
	BOD	10mg/L (6mg/L - 24mg/L)	>800 mg/L
	COD	987mg/L (785mg/L – 1,430mg/L)	> 2,000 mg/L
	Oil & Grease	<5mg/L (<5mg/L - <5mg/L)	> 20 mg/L
	Boron	5,143μg/L (4,530μg/L – 6,050μg/L)	>7,000 μg/L
	Iron	1.44mg/L (1.21mg/L – 1.74mg/L)	> 7.5 mg/L
	Cadmium	<1.0µg/L (<1.0µg/L - <1.0µg/L)	>1 µg/L
	Chromium	129μg/L (112μg/L – 146μg/L)	$> 400 \ \mu g/L$
	Copper	43μg/L (24μg/L – 61μg/L)	$> 1,000 \ \mu g/L$
	Nickel	114µg/L (98µg/L – 124µg/L)	> 800 µg/L
	Zinc	57μg/L (40μg/L – 100μg/L)	> 800 µg/L

All the leachate levels and effluent quality monitoring results were below the Limit Levels in the reporting period. No action is thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex F*2.

#### 2.3.3 Groundwater Monitoring

#### Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project with incorporation of the proposed updates under the Amendment Summary approved by EPD on 15 June 2020, groundwater monitoring was carried out at 14 perimeter groundwater monitoring wells (including 5 up-gradient wells and 9 downgradient wells) (i.e. MWX-1 to MWX-14) to monitor the groundwater quality and level of the perimeter groundwater monitoring wells at monthly interval.

The Limit Levels for groundwater quality is provided in *Table 2.24* below.

Location	Limit Levels		
	Ammoniacal-nitrogen (mg L-1)	COD (mg L <sup>-1</sup> )	
MWX-1	5.00	30	
MWX-2	5.00	30	
MWX-3	5.00	30	
MWX-4	7.63	36	
MWX-5	5.00	30	
MWX-6	5.00	46	
MWX-7	6.55	36	
MWX-8	15.85	50	
MWX-9	7.30	71	
MWX-10	5.00	30	
MWX-11	5.00	30	
MWX-12	5.00	30	
MWX-13	5.00	30	
MWX-14	5.00	30	

A bladder pump with Teflon sampling tube and adjustable discharge rates was used for purging and taking of groundwater sample from the monitoring wells. Filtered groundwater samples was collected by connecting a disposable in-line filter system to the tubing of the sampling pump, prior to storage and analysis by ALS Technichem (HK) Pty Ltd. (HOKLAS Registration No. 066).

A portable dip meter with 5mm accuracy was used for measurement of groundwater level at each well. The dip meter have an audio indicator of the water level and was checked before use.

The measurements of pH and electrical conductivity (EC) were undertaken *in situ*. *In situ* monitoring instruments in compliance with the specifications listed under Section 4.3.2 of the updated EM&A Manual were used to undertake the groundwater quality monitoring for the Project.

Details of the equipment used and the monitoring locations are summarised in *Table 2.25* and illustrated in *Figure 2.1*, respectively.

Monitoring Location	Frequency	Param	leter	Monitoring Dates	Equipment
U	Monthly	<ul> <li>Water level</li> <li>pH</li> <li>EC</li> <li>COD</li> <li>BOD5</li> <li>TOC</li> <li>Ammoniacal- nitrogen</li> <li>Nitrate- nitrogen</li> <li>Nitrite- nitrogen</li> <li>Nitrite- nitrogen</li> <li>TKN</li> <li>TN</li> <li>Sulphate</li> <li>Sulphide</li> </ul>	<ul> <li>Chloride</li> <li>Sodium</li> <li>Potassium</li> <li>Calcium</li> <li>Magnesium</li> <li>Nickel</li> <li>Manganese</li> <li>Chromium</li> <li>Cadmium</li> <li>Copper</li> <li>Lead</li> <li>Iron</li> <li>Zinc</li> <li>Mercury</li> <li>Boron</li> </ul>	Dates           7-8 Dec 2021	YSI Professional DSS (S/N: 17B102764)
		<ul><li>Carbonate</li><li>Bicarbonate</li><li>Phosphate</li></ul>			

### Table 2.25Groundwater Monitoring Details

### Monitoring Schedule for the Reporting Month

The schedule for groundwater quality monitoring during the reporting period is provided in *Annex C*.

### Results and Observations

The groundwater quality monitoring results and detailed monitoring results are summarised in *Table 2.26* and provided in *Annex F5*, respectively.

Location	Ammoniacal-nitroge	Ammoniacal-nitrogen (mg L-1)		
	<b>Monitoring Results</b>	Limit Levels	<b>Monitoring Results</b>	Limit Levels
MWX-1	0.29	5.00	11	30
MWX-2	0.02	5.00	3	30
MWX-3	1.33	5.00	19	30
MWX-4	6.79	7.63	36	36
MWX-5	1.95	5.00	28	30
MWX-6	3.52	5.00	56	46
MWX-7	5.42	6.55	23	36
MWX-8	12.50	15.85	44	50
MWX-9	5.34	7.30	20	71
MWX-10	0.03	5.00	6	30
MWX-11	0.02	5.00	4	30
MWX-12	<0.01	5.00	<2	30
MWX-13	0.04	5.00	<2	30

Limit Levels exceedance was recorded for groundwater monitoring in the reporting period and actions in accordance with the Event and Action Plan presented in *Annex F2* were undertaken. Investigation of the Limit Levels exceedance was conducted and the investigation report is presented in *Annex F6*.

<2

30

5.00

Based on the investigation conducted for the monitoring event with potential Limit Levels exceedance with the Contractor and the IEC, the groundwater quality (COD) exceedance at MWX-6 on 8 December 2021 was considered non Project-related. The Contractor was reminded to implement all relevant mitigation measures for the construction and operation works and maintain good site practice. The ET will keep track on the monitoring data and ensure Contractor's compliance of the environmental requirements.

#### 2.4 LANDFILL GAS MONITORING

**MWX-14** 

< 0.01

#### 2.4.1 Monitoring Requirements

According to the updated EM&A Manual of the Project, landfill gas monitoring was carried out at the perimeter of the waste boundary (monitoring wells), area between the SENTX Site boundary and the waste boundary (surface emission), occupied on-site building, service voids, utilities pit and manholes in the vicinity of the SENTX (build-up of landfill gas) during the operation/restoration phase.

The Limit Levels for landfill gas monitoring is provided in *Table 2.27* below.

Parameters	Monitoring Location	Limit Level (% (v/v))	
Perimeter Landfill Gas Mor	nitoring Wells (a)		
Methane & Carbon Dioxide		Methane	Carbon Dioxide
	LFG1	1.0	2.2
	LFG2	1.0	4.2
	LFG3	1.0	6.3
	LFG4	1.0	7.0
	LFG5	1.0	3.4
	LFG6	1.0	9.1
	LFG7	1.0	1.5
	LFG8	1.0	1.7
	LFG9	2.5	1.7
	LFG10	1.0	1.6
	LFG11	3.0	2.0
	LFG12	13.2	1.5
	LFG13	22.5	2.7
	LFG14	1.0	1.6
	LFG15	18.2	2.0
	LFG16	1.0	1.7
	LFG17	10.5	2.1
	LFG18	2.3	1.9
	LFG19	6.3	3.1
	LFG20	1.0	4.2
	LFG21	1.0	4.3
	LFG22	1.0	3.9
	LFG23	1.0	10.3
	LFG24	1.0	4.0
	GP1	1.0	8.5
	GP2 (shallow)	1.0	11.4
	GP2 (deep)	1.0	10.4
	GP3 (shallow)	1.0	3.9
	GP3 (deep)	1.0	1.9
	GP4 (shallow)	1.0	2.3
	GP4 (deep)	1.0	5.6
	GP5 (shallow)	1.0	9.5
	GP5 (deep)	1.0	7.5
	GP6	1.0	7.8
	GP7	1.0	4.5
	GP12	1.0	2.3
	GP15	1.0	2.2
	P7	1.0	2.5
	P8	1.0	1.7
	Р9	1.0	2.7

### Service Voids, Utilities Pits and Manholes

Methane (or flammable gas) Service voids, utilities 1% by volume pits and manholes

Parameters	Monitoring Location	Limit Level (% (v/v))
Permanent Gas Monitoring	System	
Methane (or flammable gas)	Permanent Gas Monitoring System	1% by volume (20% LEL)
Notes:		

Notes:

(a) Provisional Limit Levels established based on the pre-operation phase baseline and additional landfill gas monitoring results in the Pre-operation Baseline Monitoring Report.

Gas analysers in compliance with the specifications listed under Section 5.4.1 of the updated EM&A Manual were used to monitor the gas parameters at the landfill gas monitoring wells, service voids, utilities pits and manholes. The gas analyser was calibrated by a laboratory accredited under HOKLAS at yearly intervals and checked before use to ensure the validity and accuracy of the results. A portable dip meter was used to monitor the water level in the monitoring wells.

Permanent gas monitoring systems with pre-set alarm levels for methane at 20% lower explosive limit (LEL, equivalent to 1% methane gas (v/v)) were installed and operated in all occupied on-site buildings at SENTX. A central control panel is equipped to alert site personnel when the gas concentration at any detector reaches the alarm level.


The equipment used in the landfill gas monitoring programme is summarised in *Table 2.28*. The landfill gas monitoring locations for perimeter landfill gas monitoring wells and service voids, utilities and manholes along the Site boundary and within the SENTX site are illustrated in *Figure 2.3* and *Annex G1*, respectively.

Monitoring Location	Frequency	Parameter	Monitoring Dates	Equipment
Perimeter landfill gas monitoring wells (LFG1 to LFG24, P7 to P9, GP1 to GP7, GP12 and GP15)	Monthly	<ul> <li>Methane</li> <li>Carbon dioxide</li> <li>Oxygen</li> <li>Atmospheric pressure</li> </ul>	14 Dec 2021	GA5000 (S/N: G507306)
Service voids, utilities and manholes along the Site boundary and within the SENTX Site (UU1 to UU28)	Monthly	<ul><li>Methane</li><li>Carbon dioxide</li><li>Oxygen</li></ul>	16 Dec 2021	GA5000 (S/N: G507306)
Permanent gas monitoring system in all occupied on-site buildings	Continuous	<ul> <li>Methane (or flammable gas) by permanent gas monitoring system</li> </ul>	1 – 31 Dec 2021	Permanent gas monitoring system

### Table 2.28Landfill Gas Monitoring Details

Monitoring Schedule for the Reporting Month

The schedule for dust monitoring during the reporting period is provided in *Annex C*.

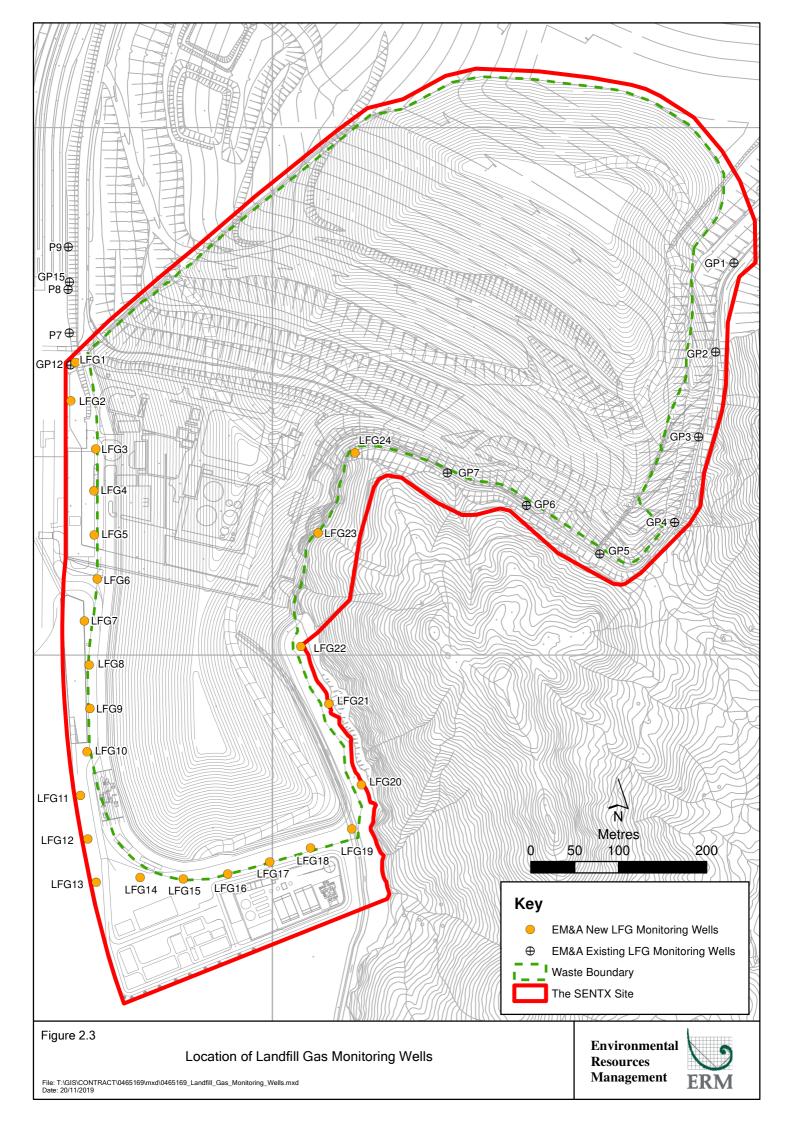

### Results and Observations

The landfill gas monitoring results are summarised and provided in *Tables* 2.29 - 2.30 and Annex G2, respectively.

Location	Methane (% (v	/v))	Carbon Dioxide (% (v/v))	
	Monitoring Results	Limit Levels <sup>(a)</sup>	Monitoring Results	Limit Levels <sup>(a</sup>
LFG1	0.0	1.0	0.1	2.2
LFG2	0.0	1.0	0.1	4.2
LFG3	0.0	1.0	0.9	6.3
LFG4	0.0	1.0	0.0	7.0
LFG5	0.0	1.0	0.2	3.4
LFG6	0.0	1.0	0.1	9.1
LFG7	0.0	1.0	0.0	1.5
LFG8	0.0	1.0	0.0	1.7
LFG9	0.0	2.5	0.1	1.7
LFG10	0.0	1.0	0.0	1.6
LFG11	0.0	3.0	0.1	2.0
LFG12	0.0	13.2	0.0	1.5
LFG13	19.6	22.5	0.0	2.7
LFG14	0.0	1.0	0.0	1.6
LFG15	1.8	18.2	0.4	2.0
LFG16	0.0	1.0	0.1	1.7
LFG17	0.0	10.5	0.2	2.1
LFG18	0.0	2.3	0.1	1.9
LFG19	0.0	6.3	0.1	3.1
LFG20	0.0	1.0	1.1	4.2
LFG21	0.0	1.0	2.0	4.3
LFG22	0.0	1.0	1.0	3.9
LFG23	0.0	1.0	2.1	10.3
LFG24	0.0	1.0	0.9	4.0
GP1	0.2	1.0	5.2	8.5
GP2 (shallow)	0.5	1.0	0.3	11.4
GP2 (deep)	0.2	1.0	0.1	10.4
GP3 (shallow)	0.3	1.0	2.5	3.9
GP3 (deep)	0.1	1.0	0.2	1.9
GP4 (shallow)	0.6	1.0	0.7	2.3
GP4 (deep)	0.7	1.0	1.7	5.6
GP5 (shallow)	0.1	1.0	5.4	9.5
GP5 (deep)	0.1	1.0	0.3	7.5
GP6	0.0	1.0	5.6	7.8
GP7	0.0	1.0	0.1	4.5
GP12	0.0	1.0	0.0	2.3
GP15	0.0	1.0	0.0	2.2
P7	0.0	1.0	0.0	2.5
P8	0.0	1.0	0.0	1.7
P9	0.0	1.0	0.0	2.7

# Table 2.29Summary of Landfill Gas Monitoring Results at Perimeter LFG Monitoring<br/>Wells in the Reporting Period

Notes:

(a) Provisional Limit Levels established based on the pre-operation phase baseline and additional landfill gas monitoring results in the Pre-operation Baseline Monitoring Report.

Location	Methane (% (v/v))				
	Monitoring Results	Limit Levels			
UU01	0.1	1.0			
UU02	0.0	1.0			
UU03	0.0	1.0			
UU04	0.1	1.0			
UU05	0.0	1.0			
UU06	0.0	1.0			
UU07	0.1	1.0			
UU08	0.0	1.0			
UU09	0.2	1.0			
UU10	0.1	1.0			
UU11	Inaccessible due to on-going construction work	1.0			
UU12	Inaccessible due to on-going construction work	1.0			
UU13	Inaccessible due to on-going construction work	1.0			
UU14	Inaccessible due to on-going construction work	1.0			
UU15	0.1	1.0			
UU16	0.1	1.0			
UU17	0.3	1.0			
UU18	0.1	1.0			
UU19	0.0	1.0			
UU20	0.1	1.0			
UU21	0.0	1.0			
UU22	0.0	1.0			
UU23	0.0	1.0			
UU24	0.0	1.0			
UU25	0.0	1.0			
UU26	0.0	1.0			
UU27	0.0	1.0			
UU28	0.0	1.0			

Table 2.30	Summary of Landfill Gas Monitoring Results at Service Voids, Utilities Pits
	and Manholes in the Reporting Period

The alarm of the permanent gas monitoring systems with pre-set levels for methane at 20% lower explosive limit (LEL, equivalent to 1% methane gas (v/v)) was not triggered at all occupied on-site buildings at SENTX in November and December 2021.

All the landfill gas monitoring results were below the Limit Levels in the reporting period. No action is thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex G3*.

### 2.5 LANDSCAPE AND VISUAL MONITORING

### 2.5.1 Monitoring Requirements

According to the updated EM&A Manual of the Project, the monthly landscape and visual audit was conducted on 26 October, 19 November and 22 December 2021 to monitor the implementation of the landscape and visual mitigation measures during construction and operation/ restoration phase. All relevant environmental mitigation measures listed in the approved EIA Report and the updated EM&A Manual and their implementation status are summarised in *Annex B*.

### 2.5.2 Results and Observations

The Contractor has implemented environmental mitigation measures as stated in the approved EIA Report and the EM&A Manual.

Regarding the landscape and visual audit, the Contractor was reminded to maintain the advance screen planting works as soon as possible to ensure effective screening of views of project works from the High Junk Peak Trail. The Contractor has considered the mitigation measures during the design phase, including the preparation of the Construction Drawings and Detailed Landscape Design Drawings.

### 2.6 EM&A SITE INSPECTION

Site inspections were carried out on a weekly basis with the Contractor, IEC and ER to monitor the implementation of proper environmental pollution control and mitigation measures for air quality, noise, surface water quality and waste management under the Project. In the reporting period, 13 site inspections were carried out on 7, 15, 21 and 28 October, 4, 11, 17 and 26 November and 2, 9, 16, 23 and 30 December 2021.

Key observations during the site inspections are summarized in *Table 2.31*.

## Table 2.31Key Observations Identified during the Site Inspections in this Reporting<br/>Period

Inspection Date	Environmental Observations and Recommendations
7 October 2021	• The Contractor shall enhance watering around the site, especially at
	Cell4X and near existing LFG plant.
	• The Contractor shall provide drip trays for the chemical stored near
	existing LFG plant and new container area.
	The Contractor shall remove the stagnant water accumulated near
	site entrance and spray larvicides for mosquito control, if necessary.
	• The Contractor shall maintain the wheel washing facilities at the site
	exit to ensure it is functioning properly at all times.
	The Contractor shall remove the general refuse accumulated near
	new container area and at the temporary drains and dispose of the
	waste regularly.
15 October 2021	The Contractor shall ensure that the Wetseps are functioning
	properly at all times and all surface water discharged at DP4T and
	DP6 is treated before discharge.
	<ul> <li>The Contractor shall clean up the oil spillage near DP6 and handle</li> </ul>
	the clean-up materials as chemical waste.
	• The Contractor shall provide drip trays for the chemicals stored near
	MSE wall, new container area and X9B.
	• The Contractor shall remove the stagnant water accumulated at the
	drip tray near new container area and treat the clean-up materials as
	chemical waste.

Inspection Date	Environmental Observations and Recommendations
21 October 2021	• The Contractor shall fix the oil interceptor at DP4T Wetsep outlet to
	ensure that all surface water is treated by the oil interceptor before
	discharge.
	• The Contractor shall display NRMM labels on the generator near site
	entrance and excavator near sump house 3.
	• The Contractor shall remove the deposited silt and grit accumulated
	at DP6 regularly to ensure it is functioning properly at all times.
	• The Contractor shall provide drip trays for the chemicals stored at
	new container area and remove the stagnant water accumulated in
	the drip trays near Cell4X and site entrance and treat the clean-up
	materials as chemical waste.
	• The Contractor shall dispose of the emptied chemical container in the
	refuse skip near DP4T as chemical waste in the chemical waste
	cabinet.
	• The Contractor shall remove the general refuse accumulated near site
	entrance and new container area and dispose of the waste regularly
	to minimise odour and pest issues.
28 October 2021	The Contractor shall fix the oil interceptor at DP4T Wetsep outlet to
20 000001 2021	ensure that all surface water is treated by the oil interceptor before
	discharge.
	<ul> <li>The Contractor shall clean up the oil spillage near site entrance and</li> </ul>
	existing LFG plant and handle the clean-up materials as chemical
	waste.
	<ul> <li>The Contractor shall provide proper drip trays for the chemicals</li> </ul>
	stored at new container area and LTP and the generator near EPD
	building. The Contractor shall also remove the stagnant water
	accumulated in the drip trays near sump house 2 and EPD building
	and treat the clean-up materials as chemical waste.
	<ul> <li>The Contractor shall maintain the signage of the chemical waste</li> </ul>
	cabinet at new container area in accordance with the COP.
	<ul> <li>The Contractor shall remove the general refuse accumulated around</li> </ul>
	the site, especially near DP4T Wetsep, guardhouse and EPD building
	and dispose of the waste regularly to minimise odour and pest
	issues.
4 November 2021	The Contractor shall replace the faded NRMM label displayed on the
4 November 2021	cherry picker near future weighbridge.
	<ul> <li>The Contractor shall maintain site drainage and remove the stagnant</li> </ul>
	water and algae accumulated at the temporary drain at new
	container area and spray larvicides for mosquito control, if
	necessary.
	<ul> <li>The Contractor shall clean up the oil spillage at Southern perimeter</li> </ul>
	bund and near EPD building and handle the clean-up materials as
	chemical waste.
	<ul> <li>The Contractor shall remove the concrete residue at the concrete</li> </ul>
	truck washing area to ensure that all wash-water is properly
	contained.
	<ul> <li>The Contractor shall maintain the signage of the chemical waste</li> </ul>
	cabinet at new container area in accordance with the COP.
	<ul> <li>The Contractor shall dispose of the emptied chemical containers near</li> </ul>
	• The Contractor shall dispose of the emplied chemical containers hear EPD building as chemical waste.
	-
	The Contractor shall remove the general refuse accumulated at new container area and dispose of the waste regularly to minimize adour
	container area and dispose of the waste regularly to minimise odour
	and pest issues.

Inspection Date	Environmental Observations and Recommendations
11 November 2021	• The Contractor shall spray water on the surface continuously during
	rock breaking operation at the buttress wall to minimise dust impact.
	• The Contractor shall cover the cement stored at new container area to
	minimise dust impact.
	• The Contractor shall clean up the oil spillage at the breaker near
	future guardhouse and at the EVA and handle the clean-up materials
	as chemical waste.
	• The Contractor shall provide drip trays for the chemicals stored near
	buttress wall.
	• The Contractor shall maintain the signage of the chemical waste
	cabinet at new container area in accordance with the COP.
17 November 2021	• The Contractor shall clean up the oil spillage at the breaker near
	town gas plant and handle the clean-up materials as chemical waste.
	• The Contractor shall remove the stagnant water accumulated at the
	drip tray near DP6 and treat the clean-up material as chemical waste.
	• The Contractor shall remove the general refuse accumulated near
	DP4T, main haul road, weighbridge, town gas plant, drainage
	channel near maintenance building and DP6.
26 November 2021	• The Contractor shall clean up the oil/ chemical spillage at the
	generator near DP6 and handle the clean-up materials as chemical
	waste.
	• The Contractor shall provide drip trays for the chemicals stored near
	guardhouse and sediment trap.
	• The Contractor shall dispose of the waste accumulated at the refuse
	skips near DP4T and DP6 regularly to minimise odour and pest
	issues.
2 December 2021	• The Contractor shall clean up the oil spillage at sediment trap and
	handle the clean-up materials as chemical waste.
	• The Contractor shall trim the climbing plants around the
	transplanted trees near DP6 regularly.
9 December 2021	• The Contractor shall provide drip trays for the chemicals stored near
	EPD building, diesel fuel tank and at Cell 1X slope.
	• The Contractor shall provide drip trays for the chemicals stored near
	EPD building, diesel fuel tank and at Cell 1X slope.
16 December 2021	The Contractor shall replace the faded NRMM labels displayed on
	the excavators near Cell 4X and EPD building.
	• The Contractor shall remove the general refuse accumulated near
	town gas plant and at the sediment trap and dispose of the waste
	regularly.
23 December 2021	• The Contractor shall replace the faded NRMM label displayed on the
	excavator near Cell 4X.
	• The Contractor shall remove the general refuse accumulated near
	water services house and dispose of the waste regularly.
	• The Contractor shall cover/ remove the stockpile of dusty materials
	near EPD building to minimise dust impact.
30 December 2021	The Contractor shall clean up the oil spillage at the generators near
	GVL building and handle the clean-up materials as chemical waste.
	<ul> <li>The Contractor shall remove the general refuse accumulated in the</li> </ul>
	refuse skip near LTP regularly to minimise odour and pest issues.
	<ul> <li>The Contractor shall remove the stagnant water accumulated at the</li> </ul>
	channel near sump house 3 and spray larvicides for mosquito
	control, if necessary.
	controly if necessary.

The Contractor has rectified all of the observations identified during environmental site inspections in the reporting period. Key environmental deficiencies identified and the corresponding rectification actions are presented in *Table 2.32*.

Deficiencies	<b>Rectifications Implemented</b>	Proposed Additional Control Measures
Surface Water		
Intercepting channels & drainage system	Reviewed drainage plan.	<ul> <li>Provision of additional drainage channels.</li> <li>Expedite the construction of permanent sediment trap and discharge culverts.</li> </ul>
DP channels (design & regular silt removal)	<ul> <li>Carried out regular maintenance and cleaning of channels.</li> <li>DP4 channel: Area near the channel was paved with concrete and a bund was built.</li> <li>DP6 channel: Gravel piles on the channel were covered with concrete which serve as blocks for running water and to divide the channel into several sections. A pump was placed in the water zone in the upstream section to pump water to the Wetsep for treatment prior to the discharge to the last section before the weir plate.</li> <li>DP6: Pipes through the gravel piles between different channel sections were covered with geotextiles to block debris and silt.</li> </ul>	N.A.
Stockpiles & exposed soil	• Installed silt fencing near surface water channel along DP6 channel.	<ul><li>Improve soil covering.</li><li>Compaction and cover for stockpiles and soil slopes.</li></ul>
Wetsep (treatment capacity & number)	<ul> <li>Reviewed Wetsep capacity.</li> <li>Chemicals dosage of the Wetsep was increased to enhance the efficiency.</li> </ul>	• Install additional Wetsep.
Backflow / ponding during heavy rainfall	• Raised with EPD (LDG) and CEDD.	N.A.

## Table 2.32Summary of Environmental Deficiencies Identified and Corresponding<br/>Additional Control Measures

### 2.7 WASTE MANAGEMENT STATUS

The Contractor has registered as a chemical waste producer under the Contract. Sufficient numbers of receptacles were available for general refuse collection and sorting.

As informed by the Contractor, waste generated during this reporting period include mainly inert C&D materials. Reference has been made to the waste flow table prepared by the Contractor. The quantities of different types of wastes and imported fill materials are summarised in *Table 2.33*.

### Table 2.33Quantities of Different Waste Disposed and Imported Fill Materials

Month/ Year	Inert C&D Materials <sup>(a)</sup> (in '000m <sup>3</sup> )	Imported Fill (in '000kg) <sup>(b)</sup> Rock Soil		Inert Construction Waste Re- used (in '000m <sup>3</sup> )	Non-inert Construction Waste <sup>(c)</sup> (in '000m <sup>3</sup> )	Recyclable Materials <sup>(d)</sup> (in '000kg)	Chemical Wastes (in '000kg)	
Oct 2021	0.710	<b>коск</b> 0	1912.010	0	0.053	0	0	
Nov 2021	3.152	0	1378.680	0	0.121	222.310	0	
Dec 2021	0.412	0	2043.810	0	0.058	11.660	0.800	

Notes:

(a) Inert construction wastes include hard rock and large broken concrete, and materials disposed as public fill. Density assumption: 1.6 (kg/L) for public fill.

(b) Imported fill refers to materials generated from other project for on-site reuse.

(c) Non-inert construction wastes include general refuse disposed at landfill. Density assumption: 0.9 (kg/L) for general refuse.

(d) Recyclable materials include metals, paper, cardboard, plastics and others.

### 2.8 IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

A summary of the Environmental Mitigation Implementation Schedule is presented in *Annex B*. The necessary mitigation measures were implemented properly for the Project.

# 2.9 SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMANCE LIMIT

The construction and operation/ restoration phase noise and landfill gas monitoring results complied with the Action and Limit Levels in the reporting period. One exceedance of the Limit Level for TSP and one exceedance of the Limit Level for landfill gas flare stack emission (CO) were recorded for air quality impact monitoring in the reporting period. The TSP exceedance at AM4 on 13 December 2021 was considered non Project-related upon further investigation. The landfill gas flare stack emission (CO) exceedance on 17 December 2021 was found to be Project-related. One exceedance of the Limit Level for groundwater (COD) was recorded for water quality impact monitoring in the reporting period. The groundwater (COD) exceedance at MWX-6 on 8 December 2021 was considered non Project-related upon further investigation.

Cumulative statistics on exceedances is provided in *Annex H*.

### 2.10 SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

There were no complaints, notification of summons or prosecution recorded in the reporting period. Statistics on complaints, notifications of summons and successful prosecutions are summarised in *Annex H*.

### CONCLUSION AND RECOMMENDATION

3

This Quarterly EM&A Report presents the findings of the EM&A activities undertaken during the period from 1 October to 31 December 2021 in accordance with the updated EM&A Manual and the requirements of the Environmental Permit (*EP-308/2008/B*).

Air quality (24-hour TSP, odour, thermal oxidiser, landfill gas flare and landfill gas generator stack emission), noise, water quality (surface water, leachate and groundwater) and landfill gas monitoring were carried out in the reporting period. Results for noise and landfill gas monitoring complied with the Action and Limit Levels in the reporting period. One exceedance of the Limit Level for TSP, one exceedance of the Limit Level for landfill gas flare stack emission (CO) and one exceedance of the Limit Level for groundwater (COD) were recorded in the reporting period.


Thirteen environmental site inspections were carried out during the reporting period. Environmental deficiencies were identified during the site inspection and the Contractor has proposed additional control measures to rectify the deficiencies.

There were no complaints, notification of summons or prosecution recorded in the reporting period.

It is noted that most environmental pollution control and mitigation measures were properly implemented and the construction and operation activities of the Project did not introduce any adverse impact to the sensitive receivers in the reporting period. Yet, some environmental deficiencies were identified during the reporting period and additional control measures have been proposed by the Contractor to rectify the corresponding deficiencies. The monitoring programme has been reviewed and was considered as adequate to cater for the nature of works in progress. Change to the monitoring programme was thus not recommended at this stage. The monitoring programme will be evaluated as appropriate in the next reporting period. The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures. Annex A

## Work Programme

<b># W</b>	/BS Path Activity Activity Name	Dur Start Finish Total Predecessor Details Successor Details Float	2018 2021 2023 2023 2023 2023 2023 2023 2023
336 337		Float	Q2 Q3 Q4 Q1 Q2 Q3
338 339			
340 341 342			
342 343 344 345			
345 346 347			
348 349			
350 351			
352 353	SA2.5 Construction (Initial Works) SA2.5.02 Advance Works & Site Establishment SA2.5.02.01 Site Establishment & Mobilization	1153       12-Apr-18       07-Jun-21       705         1148       12-Apr-18       02-Jun-21       35         222       42-Apr-14       40-Mar 40       200	
355 355 356	SA2.3.02.01         Site Establishment & Mobilization           5.02.01         52-1000         Site Mobilization for Parts X1 & X2           5.02.01         52-1100         Site Mobilization for Parts X3, X4 & X5	333         12-Apr-18         10-Mar-19         820         Control           30         31-Dec-18         29-Jan-19         820         11-1100: FS, 11-1200: FS         52-1300: FS, M 3. 1: FS, M 3. 2: FS           30         12-Apr-18         11-May-18         1083         11-1300: FS, 11-1400: FS, 11-1500: FS         52-1300: FS, M 3. 1: FF	
357 358	5.02.0152-1200Temporary Office for Employer / ER / IC5.02.0152-1300Hoarding and Fencing Works	60         10-Oct-18         08-Dec-18         0         23-1300: FS         11-1700: SS, M 3. 1: FS           40         30-Jan-19         10-Mar-19         820         52-1000: FS, 52-1100: FS         32-1500: FS, M10. 1: FS -26, M10. 2: F	FS -13, M10. 3: FS
359 360	SA2.5.02.02     Site Survey & Investigation Works for Parts X1 & X2       5.02.02     52-1400     Condition Survey	50         31-Dec-18         18-Feb-19         840         11-1100: FS, 11-1200: FS         52-1600: FS	
361 362	5.02.02     52-1500     Topographic Survey       5.02.02     52-1600     Site inspection, Review of Condition Survey Report	20         31-Dec-18         19-Jan-19         845         11-1100: FS, 11-1200: FS         52-1600: FS           25         25-Jan-19         18-Feb-19         840         52-1500: FS, 52-1400: FS         32-1500: FS	
363 364 365	SA2.5.02.03       Site Survey & Investigation Works for Parts X3, X4 & X5         5.02.03       52-1700       Condition Survey         5.02.03       52-1800       Topographic Survey	50         12-Apr-18         31-May-18         1103         Image: Constraint of the state of the stat	
366 367	5.02.03       52-1900       Site inspection, Review of Condition Survey Report         SA2.5.02.04       Environmental Monitoring	25       07-May-18       31-May-18       1103       52-1700: FS, 52-1800: FS       32-1500: FS         975       02-Oct-18       02-Jun-21       35       4	
368 369	5.02.04       52-2000       Installation of Monitoring Stations & Wells (GP & GW)         5.02.04       52-2100       Installation of Monitoring Stations & Wells (GP & GW) on Buttress Wall         5.02.04       52-2200       Conduct Baseline Monitoring for Construction (one month)	120         02-Oct-18         29-Jan-19         0         23-1600: FS         52-2200: SS 60           120         02-Oct-18         29-Jan-19         0         23-1600: FS         52-2200: SS 60           30         01-Dec-18         30-Dec-18         0         52-2200: SS 60, 52-2100: SS 60         11-1100: FS	
370	5.02.04       52-2200       Conduct Baseline Monitoring for Operation (one year)         SA2.5.03       Civil Engineering Works	30       01-Dec-18       30-Dec-18       0       52-2000: SS 60, 52-2100: SS 60       11-1100: FS         365       03-Jun-20       02-Jun-21       35       32-1500: FS -400, 53-4500: FS       12-1400: FS         748       13-Jan-19       29-Jan-21       834       64       14-1400: FS	
373 374	SA2.5.03.0         Buttress Wall           5.03.0         53-1000         Section adj. SENT	475         02-Mar-19         18-Jun-20         83         6           300         13-Apr-19         06-Feb-20         96         11-1300: FS, 23-2500: FS, 53-3000: FS, 31-1200: FS, 53-1100: FS, 53-1300: FS, 53-3100: FS, 53-3100: FS, 53-1300: FS, 53-3100: FS, 53-1300: FS, 53-1300: FS, 53-3100: FS, 53-1300: FS, 5	FS, M 3. 5: FS -150, M 3.
375 376	5.03.0         53-1100         Diversion of SENT Landfill Gas Pipe           5.03.0         53-1200         Section at Cell 4	45         07-Feb-20         22-Mar-20         96         23-2500: FS, 53-1000: FS         53-1300: FS, 54-4000: FS, M 3. 3: FS           400         02-Mar-19         04-Apr-20         83         11-1300: FS, 23-2500: FS, 53-3000: FS, 11-1400: FS         53-1300: FS, 53-3100: FS, M 3. 7: FS, M 3.	
377	5.03.0 53-1300 Install Landfill Gas Pipe on Buttress Wall	75         05-Apr-20         18-Jun-20         83         41-1500: FS, 53-1100: FS, 53-1200: FS, 53-1000: FS         54-4000: FS	
378 379	SA2.5.03.1         Landfill Cell 1           5.03.1         53-1400         Earth bund (Eastern)	503         13-Jan-19         29-May-20         214         90         90         04-Aug-19         01-Nov-19         9         11-1100: FS, 23-2500: FS, 53-4200: FS, 53-2800: FS         53-2000: FS, 53-2300: FS, 53-3400: FS           63-1100: FS, 63-1200: FS, 63-1200: FS, 63-1300: FS         9         11-1100: FS, 23-2500: FS, 53-4200: FS, 53-2800: FS         53-2000: FS, 53-2300: FS, 53-3400: FS	
380	5.03.1 53-1500 Earth bund (Southern)	90         26-Apr-19         24-Jul-19         314         11-1100: FS, 23-2500: FS, 53-2800: FS         53-2000: FS, 53-2200: FS, 53-2300: FS           53-3700: FS, 53-3800: FS         53-3700: FS, 53-3800: FS         53-3700: FS, 53-3800: FS	
381 382	5.03.1         53-1600         Earth bund (Western)           5.03.1         53-1700         Intercell bund (Cell 1/2)	90       13-Jan-19       12-Apr-19       417       11-1100: FS, 23-2500: FS       53-1900: FS, 53-2000: FS, 53-2200: FS         75       13-Jan-19       28-Mar-19       432       11-1100: FS, 23-2500: FS       53-2000: FS	FS, 53-3800: FS
383	5.03.1         53-1900         Pump Station (PS#1X)	90         13-Jan-19         12-Apr-19         217         11-1100: FS, 23-2500: FS, 31-1300: FS         53-1900: FS, 63-1100: FS, 63-1200: FS           45         13-Apr-19         27-May-19         507         53-1800: FS, 53-1600: FS         53-2100: FS, 53-2200: FS	
385	5.03.1         53-2000         Lining Works	135         02-Nov-19*         15-Mar-20         214         41-1500: FS, 53-1400: FS, 53-1500: FS, 53-1600: FS, 53-2100: FS, 53-2100: FS         53-2100: FS	
386 387	5.03.1     53-2100     Protective Stone Laying & Leachate Collection Pipe       5.03.1     53-2200     Install Leachate Force Main	75         16-Mar-20         29-May-20         214         53-2000: FS, 41-1500: FS, 53-1900: FS         32-1500: FS, 54-2800: FS, M 4. 3: FS           75         25-Jul-19         07-Oct-19         449         53-1500: FS, 53-1600: FS, 41-1500: FS, 53-1900: FS         54-2800: FS	
388 389	5.03.1       53-2300       Install Landfill Gas Pipe on earth bund         5.03.1       53-2400       Leachate Pipe Connection (Cell 1 to LTP)	55         02-Nov-19         26-Dec-19         258         41-1500: FS, 53-1400: FS, 53-1500: FS         54-4000: FS           30         09-Mar-20         07-Apr-20         266         23-2500: FS, 54-1000: SS         54-2800: FS	
390 391	SA2.5.03.4 Landfill Cell 4         5.03.4       53-2500       Provide Temporary Leachate Pipe on Cell 4 Area         SA2.5.03.5       Drainage - Surface Run-Off	30         09-Jul-20         07-Aug-20         144         23-2500: FS, 63-2600: SS -90         54-2800: FS, M 3. 3: FS           740         16-Jan-19         24-Jan-21         839         54-2800: FS, M 3. 3: FS	
393 394	5.03.5         53-2600         Construct Cut-Off Channel 12A           5.03.5         53-2700         Connect Cut-Off Channel 12A to DP6	60         16-Jan-19         16-Mar-19         9         11-1100: FS, 23-2800: FS         53-2700: FS           20         17-Mar-19         05-Apr-19         9         53-2600: FS, 31-1400: FS, 23-1900: FS         53-2800: FS	
395 396	5.03.5       53-2800       Diversion from Existing Trapezoidal Channel into Channel 12A         5.03.5       53-2900       Removal of Existing Trapezoidal Channel along Eastern Bund	20         06-Apr-19         25-Apr-19         9         53-2700: FS         53-1400: FS, 53-1500: FS, 53-2900: FS           30         26-Apr-19         25-May-19         9         53-2800: FS         53-4200: FS	FS, 63-100: FS,
397 398	5.03.5       53-2900       Reinoval of Existing Trapezoldal Channel along Eastern Bund         5.03.5       53-3000       Cut-Off Channel C4 Diversion to Cut-Off Channel 17-2         5.03.5       53-3100       Cut-Off Channel X5 on Buttress Wall, Cell 4, Cell 3	30         26-Apr-19         23-Valy-19         9         33-2200. FS         53-4200. FS           45         16-Jan-19         01-Mar-19         83         11-1300: FS, 23-2800: FS         53-1000: FS, 53-1200: FS           90         05-Apr-20         03-Jul-20         289         53-1000: FS, 53-1200: FS         53-3200: FS	
399 400	5.03.553-3200Temporary Diversion Cut-Off Channel X5 to 12A5.03.553-3300Culvert X5 (5m long) & Perm Connection of Cut-Off Channel X5	20       04-Jul-20       23-Jul-20       289       53-3100: FS, 23-1900: FS       53-3300: FS, M 3. 4: FS         30       26-Dec-20       24-Jan-21       134       53-4100: FF, 63-1900: FS, 53-3200: FS       32-1500: FS	
401 402	5.03.5       53-3400       Construct Perimeter Channel X6 on Eastern Bund & Southern Bund of Cell 1         5.03.5       53-3500       Construct Perimeter Channel X6 on Eastern Bund of Cell 2         5.03.5       53-3500       Construct Perimeter Channel X6 on Eastern Bund of Cell 2	50         02-Nov-19         21-Dec-19         249         53-1400: FS, 53-1500: FS         53-3500: FS           50         20-Feb-20         09-Apr-20         189         63-1000: FS, 53-3400: FS         53-3600: FS           50         20-bit 20         09-Apr-20         189         63-1000: FS, 53-3400: FS         53-3600: FS	
403	5.03.5       53-3600       Construct Perimeter Channel X6 Eastern Bund of Cell 3         5.03.5       53-3700       Culvert X6 (25m long) at Cell 1 Southern Bund         5.03.5       53 3800       Perimeter Channel (Y9R) at Cell 1 Southern Bund	50         09-Jun-20         28-Jul-20         129         63-1900: FS, 53-3500: FS         53-3900: FS           75         25-Jul-19         07-Oct-19         1314         53-1500: FS         53-3900: FS           45         25-Jul 49         07-Sop 19         1344         53-1500: FS         53-1500: FS	
405 406	5.03.5       53-3800       Perimeter Channel (X9B) at Cell 1 Southern & Western Bund         5.03.5       53-3900       Drop Inlet & Culvert (X9) - 21m long	45         25-Jul-19         07-Sep-19         1344         53-1500: FS, 53-1600: FS           180         29-Jul-20         24-Jan-21         129         11-1100: FS, 23-1900: FS, 53-3600: FS         53-4000: FF, 53-4100: FF, 53-6000: FS           2: FS         FS         25-3000: FS         25-3000: FS         25-3000: FF, 53-4100: FF, 53-6000: FS	FS, M 9. 1: FS -90, M 9.
407	5.03.5         53-4000         Sediment Trap (ST)           5.03.5         53-4100         Dual Culvert 74m long (connect to DP4)	180       29-Jul-20       24-Jan-21       129       11-1100: FS, 23-1900: FS, 11-1200: FS, 53-3900: FF       53-6000: FS, M 9. 3: FS -90, M 9. 4: FS         180       29-Jul-20       24-Jan-21       129       11-1100: FS, 11-1200: FS, 23-1900: FS, 53-3900: FF       53-3300: FF, 53-6000: FS, M 9. 1: FS -90, M 9. 1:	
409	5.03.5       53-4100       Dual Culvert 74m long (connect to DP4)         SA2.5.03.6       Drainage - Ground Water         5.03.6       53-4200       Construct Groundwater Collection Pipe along Cells X1 & X2 Eastern Bund	180       29-Jul-20       24-Jan-21       129       11-1100: FS, 11-1200: FS, 23-1900: FS, 53-3900: FF       53-3300: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, M 9. 1: FS - 53-3000: FF, 53-6000: FS, 53-1000: FS, 53-2000: FS         200       26-May-19       03-Aug-19       9       11-1100: FS, 23-1600: FS, 53-2900: FS       53-1400: FS, 53-4300: FS, 63-1000: FS	
410	5.03.6 53-4300 Construct Groundwater Collection Pipe along Cell X3 Eastern Bund	50         04-Aug-19         22-Sep-19         159         53-4200: FS         53-4200: FS	
412 413 414	5.03.6       53-4400       Construct Groundwater Collection Pipe along Intercell Bund X2/X3         5.03.6       53-4500       Construct Manhole MH-X1         SA2.5.03.7 Utilities - Distribution within New Infrastructure Area	50       23-Sep-19       11-Nov-19       209       53-4300: FS       53-4500: FS, 63-1200: FS         30       12-Nov-19       11-Dec-19       209       53-4400: FS       52-2300: FS, M 9. 5: FS         391       11-Aug-19       04-Sep-20       276       276       276	
415 416	5.03.753-4600Power Supply HV Works (Transformer & HV switchgear)5.03.753-4700Power Distribution, LV Power Supply Works	5       30-Jun-20       04-Jul-20       0       54-3000: FS       12-1200: FS         2       05-Jul-20       06-Jul-20       0       54-3100: FS, 12-1200: FS       12-1000: FS	
417 418	5.03.7     53-4800     Sewerage (Collection to LTP)       5.03.7     53-4900     Sewerage (Discharge to Site Boundary)	60         07-Jul-20         04-Sep-20         271         54-1000: FS, 54-3100: FS, 54-3300: FS, 54-4100: FS         12-1100: FS, 53-6100: FS           60         07-Jul-20         04-Sep-20         271         54-1000: FS, 54-4100: FS, 54-4600: FS         12-1100: FS, 53-6100: FS	
419 420	5.03.7         53-5000         Lighting Provision           5.03.7         53-5100         Fire Services	30         07-Jul-20         05-Aug-20         6         54-100: FS, 54-4100: FS, 54-4600: FS         12-1100: FS, 32-2100: FS           115         12-Mar-20         04-Jul-20         2         53-6800: FS         12-1000: FS	
421 422	5.03.7         53-5200         Water Supply (Fresh & Salt)           5.03.7         53-5300         Telecom & Network	115       12-Mar-20       04-Jul-20       338       53-6600: FS, 53-6700: FS       12-1100: FS         45       11-Aug-19       24-Sep-19       622       53-6400: FS       12-1100: FS         45       22-lum 20       22-lum 20       53-6400: FS       54-6000 FS	
423 424 425	5.03.7       53-5400       Gas Network (LFG to LTP)         SA2.5.03.8 Utilities - Works Associated with Utilities Undertakers         SA2.5.03.8.U1       CLP	15       22-Jun-20       06-Jul-20       176       54-1000: FF       54-2800: FS         703       27-Feb-19       29-Jan-21       129       60-100       60-100       60-100         459       27-Feb-19       30-May-20       43       60-100       60-100       60-100       60-100	
426	5.03.8.U1 53-5500 Excavate Trench for CLP Cable	100         13-May-19         20-Aug-19         194         23-2900: FS         53-5800: FS, 54-1000: SS, 54-4100: SS         53-5800: FS, 54-1000: SS, 54-4100: SS         1: FS -60, M10. 2: FS -30, M10. 3: FS	
427 428	5.03.8.U1       53-5600       Backfill Trench after CLP Cable Laying         5.03.8.U1       53-5700       CLP Cable Laying (from CLP Substation to Site Boundary)         5.03.8.U1       53-5800       CLP Cable Laying (from Site Boundary to H)/ Switchroom)	30         01-May-20         30-May-20         43         53-5800: FS         54-1000: FF, 54-4100: FF, 54-4600: FF           200         27-Feb-19         14-Sep-19         229         32-2400: FS         54-3000: FS         54-3000: FS           60         02-Mar-20         30-Apr-20         0         53-5500: FS         53-5600: FS         53-5600: FS         53-5600: FS	
429	5.03.8.U1       53-5800       CLP Cable Laying (from Site Boundary to HV Switchroom)         5.03.8.U1       53-5900       CLP HV associated equipment installation	60       02-Mar-20       30-Apr-20       0       53-5500: FS, 54-2900: FS, 32-2400: FS, 53-5900: FF 15       53-5600: FS, 54-3000: FS         120       18-Dec-19       15-Apr-20       0       54-2900: FS, 32-2400: FS       53-5800: FF 15	
431 432	SA2.5.03.8.U2         DSD           5.03.8.U2         53-6000         Connection to Storm Drain System	147         05-Sep-20         29-Jan-21         129           5         25-Jan-21         29-Jan-21         129         53-4100: FS, 53-4000: FS, 53-3900: FS         32-1500: FS           5         05-Sep-20         00-Sep-20         271         53-4100: FS, 53-4000: FS         32-1500: FS	
433 434 435	5.03.8.U2     53-6100     Connection to Foul Drain System       SA2.5.03.8.U3     Telecom       5.03.8.U3     53-6200     Excavate Trench for PCCW	5         05-Sep-20         09-Sep-20         271         53-4800; FS, 53-4900; FS         32-1500; FS           100         13-May-19         20-Aug-19         327         53-6400; FS, 54-1000; SS, 54-4100; SS         53-6400; FS, 54-1000; SS, 54-4100; SS           60         13-May-19         11-Jul-19         307         23-2900; FS         53-6400; FS, 54-1000; SS, 54-4100; SS	
436	5.03.8.U3     53-6300     Backfill Trench after PCCW Cable Laying	10         11-Aug-19         20-Aug-19         327         53-6400: FS         54-1000: FF, 54-4100: FF, 54-4600: FF	
437 438 430	5.03.8.U3       53-6400       Laying Cables & Connection         SA2.5.03.8.U4       WSD         5.03.8.U4       53-6500       Install Watermain & Piping for Water Supplies	30         12-Jul-19         10-Aug-19         327         53-6200: FS         53-5300: FS, 53-6300: FS           304         13-May-19         11-Mar-20         338         53-600: FS, 53-6700: FS, 53-6800: FS	FS, 53-6900: FS
440	5.03.8.U4 53-6600 Connection for Fresh Water & Meter Installation	30         11-Feb-20         11-Mar-20         338         53-6500: FS, 32-2300: FS         53-5200: FS	
441 442	5.03.8.U4       53-6700       Connection for Salt Water         5.03.8.U4       53-6800       Connection for Fire Services         5.03.8.L4       53-6900       Connection for Cooling Tower & Meter Installation	30         11-Feb-20         11-Mar-20         338         53-6500: FS, 32-2300: FS         53-5200: FS           30         11-Feb-20         11-Mar-20         2         53-6500: FS, 32-2300: FS         53-5100: FS           30         11-Feb-20         11-Mar-20         11         53-6500: FS, 32-2300: FS         53-5100: FS           30         11-Feb-20         11-Mar-20         117         53-6500: FS, 32-2300: FS         54-2700: FS, 54-3900: FS	
443 444 445	5.03.8.U4       53-6900       Connection for Cooling Tower & Meter Installation         SA2.5.03.8.U5       HyD Lighting         5.03.8.U5       53-7000       Installation of Public Street Lighting / Handover	30         11-Feb-20         11-Mar-20         117         53-6500: FS, 32-2300: FS         54-2700: FS, 54-3900: FS           120         07-Jul-20         03-Nov-20         216	
446 447 448	SA2.5.04       Building Construction, incl. E&M and System Installation, and T&C         SA2.5.04.A       Part X1 Area A         5.04.A       54-1000         General Area & Access Road	890         31-Dec-18         07-Jun-21         0         0           554         31-Dec-18         06-Jul-20         36	
449	5.04.A     54-1000     General Alea & Access Road       5.04.A     54-1100     Carpark & Supporting Area	60         31-Dec-18         28-Feb-19         64         23-1300: FS, 11-1100: FS         53-5000: FS, 53-5400: FF, 53-7000: FS           31-Dec-18         28-Feb-19         64         23-1300: FS, 11-1100: FS         32-1500: FS, M 5.11: FS -30, M 5.12: F	FS, 68-1700: FS
450	5.04.A     54-1200     Diesel Fuel Tanks	60         08-May-20         06-Jul-20         36         23-1300: FS, 23-5200: FS, 12-1000: FF, 11-1100: FS         32-2200: FS	
451	5.04.A         54-1300         EPD Building           5.04.A         54-1400         Fire Service Tank	270       30-Apr-19       24-Jan-20       44       23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1700: SS 60       32-2100: FS, M 5. 4: FS -135, M 5. 5: F         270       29-Jun-19       24-Mar-20       44       23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1300: SS 60       32-2100: FS, M 5. 10: FS, 12-1000: FS, 12-1	
453	5.04.A         54-1400         File Service Tank           5.04.A         54-1500         GVL Building	270         29-301-19         24-401-20         44         25-1300. FS, 23-5200. FS, 11-1100. FS, 54-1300. SS 60         52-2100. FS, M 5. 10. FS, M 5. 11. SF 30, M 5. 2: SF           300         31-Dec-18         26-Oct-19         44         23-1300: FS, 23-5200: FS, 11-1100: FS         32-2100: FS, M 5. 1: SF 30, M 5. 2: SF           54-1700: SS 60         54-1700: SS 60         32-2100: FS, M 5. 1: SF 30, M 5. 2: SF	
454	5.04.A     54-1600     Laboratory Building       5.04.A     54-1700     Maintenance Building & Area	270       28-Aug-19       23-May-20       44       23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1400: SS 60       32-2100: FS, M 5. 6: FS -135, M 5. 7: F         270       01-Mar-19       25-Nov-19       44       23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1500: SS 60       32-2100: FS, M 5. 8: FS -135, M 5. 7: F	
456	5.04.A     54-1700     Maintenance Building & Area       5.04.A     54-1800     Storage Facility & Area	270         01-Mar-19         25-Nov-19         44         23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1500: SS 60         32-2100: FS, M 5. 8: FS -135, M 5. 9: F           60         01-Mar-19         29-Apr-19         64         23-1300: FS, 11-1100: FS, 54-1100: FS         32-1500: FS, M 5.11: FS -30, M 5.12: F           54-2000: FS         44         23-1300: FS, 11-1100: FS, 54-1100: FS         54-2000: FS         32-2100: FS, M 5.11: FS -30, M 5.12: F	
457	5.04.A         54-1900         Waste Oil Tanks           5.04.A         54-2000         Water Service House	90         08-Apr-20         06-Jul-20         36         23-1300: FS, 23-5200: FS, 12-1000: FF, 11-1100: FS         32-2200: FS	
459	5.04.A 54-2000 Water Service House SA2.5.04.B Part X1 Area B SA2.5.04.B 1 BioPlant Building	60       30-Apr-19       28-Jun-19       64       23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1800: FS       32-2100: FS, M 5.10: FS, 12-1000: FS,         890       31-Dec-18       07-Jun-21       0       0         330       17-Jan-19       12-Dec-19       243	
461	SA2.5.04.B.1       BioPlant Building         5.04.B.1       54-2100       LTP BioPlant Building         SA2.5.04.B.2       Leachate Treatment Plant	330         17-Jan-19         12-Dec-19         243           330         17-Jan-19         12-Dec-19         243         23-1300: FS, 23-5200: FS, 23-3200: FS, 11-1100: FS, 32-2200: FS, 32-2200: FS, M 6. 2: FS - 31-1000: FS           589         31-Dec-18         10-Aug-20         21         21	S-165, M 6. 3: FS
463	SA2.5.04.B.2       Leachate Treatment Plant         5.04.B.2       54-2200       Main Plant Area included Civil works	589         31-Dec-18         10-Aug-20         21           274         31-Dec-18         30-Sep-19         0         23-1300: FS, 23-3200: FS, 11-1100: FS         54-2300: FS, 54-2400: FS, 54-2500: FS           SF 30, M 6. 4: FS -137, M 6. 5: FS         SF 30, M 6. 4: FS -137, M 6. 5: FS         SF 30, M 6. 4: FS -137, M 6. 5: FS	
464	5.04.B.2         54-2300         MEP Installation           5.04.B.2         54-2400         SBR Tanks	220         01-Oct-19         07-May-20         0         41-2100: FS, 41-1800: FS, 22-2100: FS, 54-2200: FS, 12-1000: FS 60, 32-1900: FS, 54-2600: M 6. 9: FS, 32-2200: FS           100         01-Oct-19         08-Jan-20         236         41-2400: FS, 54-2200: FS         54-2600: FS, M 6. 6: FS	0: FS, M 6. 8: FS -110,
466 467	5.04.B.2         54-2400         SBR Tanks           5.04.B.2         54-2500         Ammonia Stripper           SA2.5.04.B.3         LTP - Test & Commission	100         01-Oct-19         08-Jan-20         236         41-2400: FS, 54-2200: FS         54-2600: FS, M 6. 6: FS           315         01-Oct-19         10-Aug-20         21         41-3000: FS, 54-2200: FS         54-2600: FS, M 6. 8: FS -150, M 6. 9: F           301         11-Aug-20         07-Jun-21         0         6         6	FS F
468	5.04.B.3         54-2700         Wet testing	301         11-Aug-20         07-0 u1/21         0         2           45         11-Aug-20         24-Sep-20         21         54-2300: FS, 54-2400: FS, 54-2500: FS         23-6600: FS -150, 23-6900: SS, 54-270           75         25-Sep-20         08-Dec-20         21         54-2600: FS, 12-1200: FS, 53-6900: FS, 31-2200: FS, 54-2800: FS, M11. 2: FS	700: FS, M11. 1: FS
470	5.04.B.3         54-2700         Wet testing           5.04.B.3         54-2800         Operational testing	75         25-Sep-20         08-Dec-20         21         54-2600: FS, 12-1200: FS, 53-6900: FS, 31-2200: FS, 51-2200: FS, 51-22	
471	SA2.5.04.C Part X1 Area C SA2.5.04.C.1 LFG - Power Supply Building	730         31-Dec-18         29-Dec-20         0	
472 473	SA2.5.04.C.1       LFG - Power Supply Building         5.04.C.1       54-2900       LFG Building (with Transformer Room)         5.04.C.1       54-2000       Transformer 8 bl/ (Sutisfaces lastellation)	530         17-Jan-19         29-Jun-20         5           335         17-Jan-19         17-Dec-19         0         23-1300: FS, 23-3500: FS, 11-1100: FS, 31-1000: FS         53-5800: FS, 53-5900: FS, 54-3000: FS           60         01 May 20         20 Jun 20         0         E4 2000: ES E1 2600: ES E2 2600: ES E2 2700: ES         E3 4600: ES M 7 4: ES 20 M 7 5: ES	
474 475	5.04.C.1     54-3000     Transformer & HV Swtichgear Installation       5.04.C.1     54-3100     MEP Installation, with T&C	60         01-May-20         29-Jun-20         0         54-2900: FS, 41-1200: FS, 53-5800: FS, 53-5700: FS         53-4600: FS, M 7. 4: FS -30, M 7. 5: FS           75         18-Dec-19         01-Mar-20         125         54-2900: FS         32-1400: FS, 32-2100: FS, 53-4700: FS	
476 477	SA2.5.04.C.2         LFG Treatment Plant           5.04.C.2         54-3200         Main Plant Area included Civil Works	554         31-Dec-18         06-Jul-20         0         FS - 30, M 7. 5: FS           384         31-Dec-18         18-Jan-20         0         23-3500: FS, 11-1100: FS         54-3300: FS, 54-3400: FS, 54-3500: FS	FS, 54-3600: FS,
478	5.04.C.2         54-3300         MEP Installation	54-3700: FS, 54-3800: FS, M 7. 1: SF 3           170         19-Jan-20         06-Jul-20         0         54-3200: FS, 12-1000: FF         32-2000: FS, 53-4800: FS, 54-3900: FS	<sup>3</sup> 0, M 7. 2: FS -200, M
479	5.04.C.2 54-3400 GHS600 Blower 601 A&B Relocation	15         19-Jan-20         02-Feb-20         155         23-5800: FS, 54-3200: FS         54-3900: FS, M 7. 4: FS -8, M 7. 5: FS	
480 481 482	5.04.C.2       54-3500       Pre-treatment         5.04.C.2       54-3600       Flares (incl. PLC control, interlink to Towngas PF & LTP)         5.04.C.2       54-3700       LEG Engine (incl. on-grid protection, PLC control, turning)	60         19-Jan-20         18-Mar-20         110         41-3900: FS, 54-3200: FS         54-3900: FS, M 7. 4: FS -30, M 7. 5: FS           125         19-Jan-20         22-May-20         45         41-3300: FS, 54-3200: FS         54-3900: FS, M 7. 4: FS -60, M 7. 5: FS           110         21-Feb-20         09-Jun-20         27         41-3600: FS, 54-3200: FS         54-3900: FS, M 7. 4: FS -60	
483 484	5.04.C.2       54-3700       LFG Engine (incl. on-grid protection, PLC control, turning)         5.04.C.2       54-3800       Cooling System         SA2.5.04.C.3       LFG - Test & Commission	45       19-Jan-20       03-Mar-20       125       22-1500: FS, 54-3200: FS       54-3900: FS, M 7. 4: FS -25, M 7. 5: FS         176       07-Jul-20       29-Dec-20       0       0	<u></u>
485	5.04.C.3 54-3900 MEP Testing	65         07-Jul-20         09-Sep-20         0         54-3400: FS, 54-3500: FS, 54-3600: FS, 54-3700: FS, 51-2200: FS, 51-220	
486	5.04.C.3     54-4000     Operational Testing	111         10-Sep-20         29-Dec-20         0         53-1300: FS, 63-2700: FS, 63-1800: FS, 53-2300: FS, 53-23	FF, 63-4900: FS,
487	SA2.5.04.D Part X1 Area D	374 29-Jun-19 06-Jul-20 6	

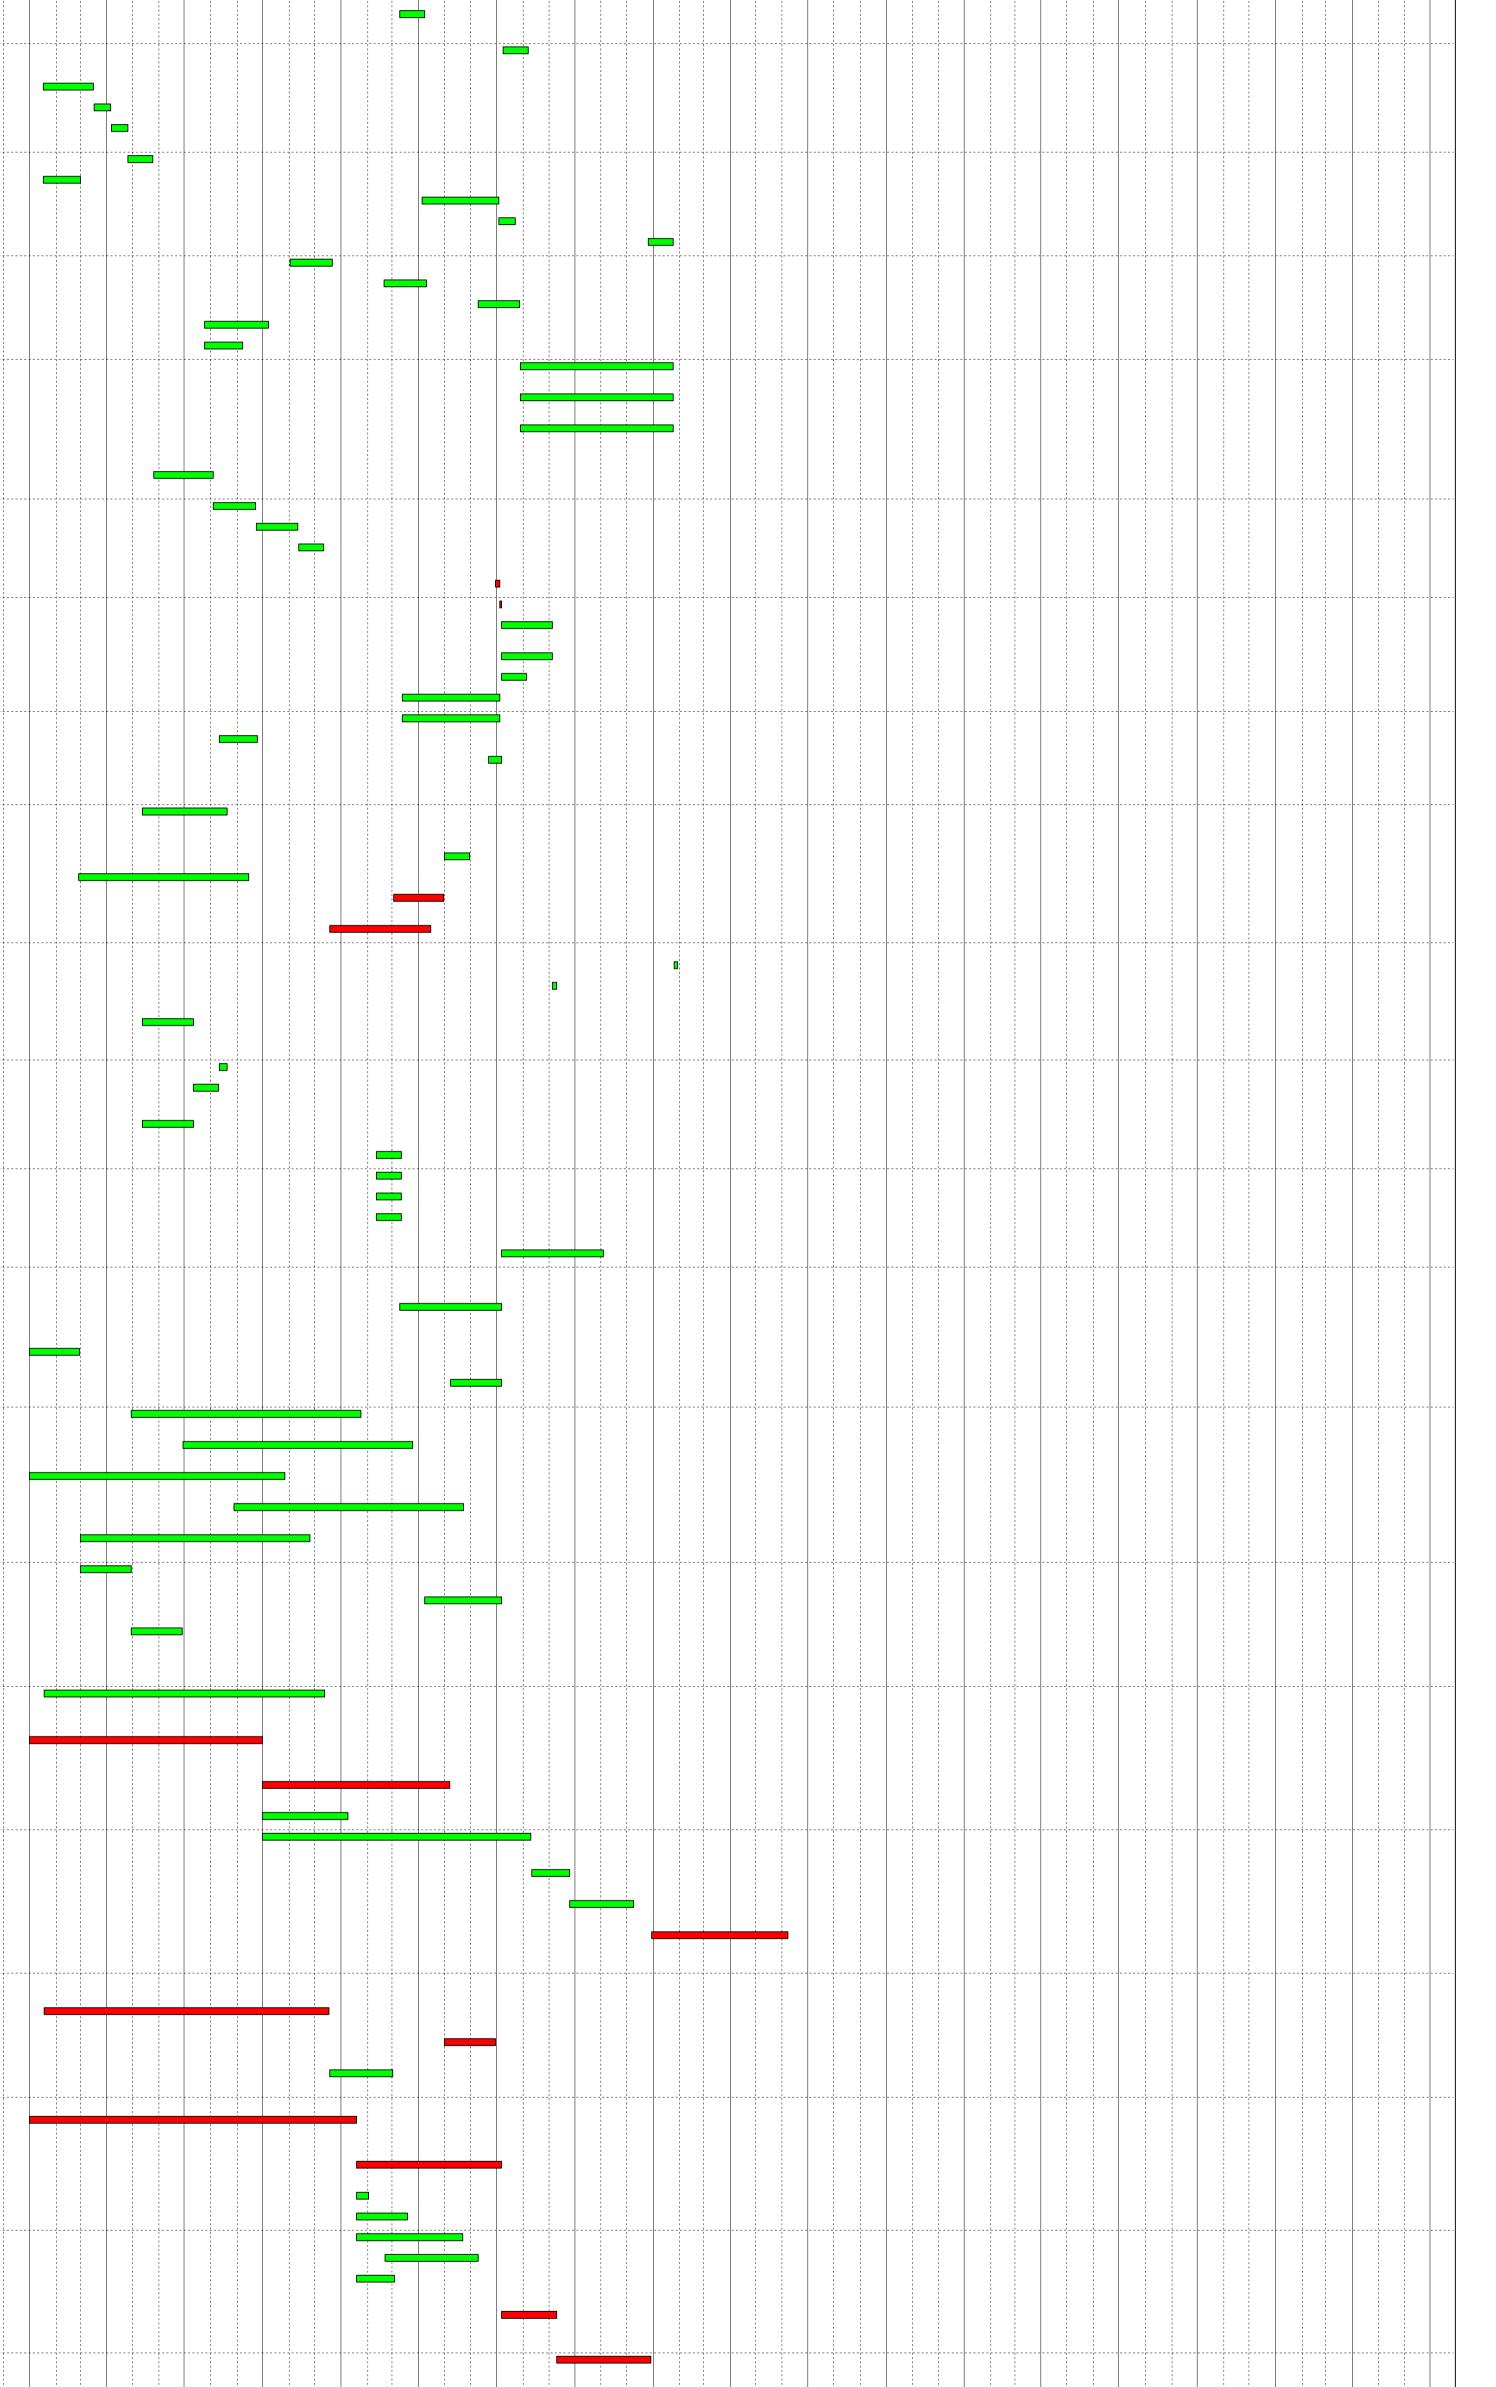

<ul> <li>Milestone</li> </ul>				
	ical Remaining Work	Page : 3 of 4	4	
	Remaining Work			South-East Ne
				0.0000.10,00-4000.10,1012.4.10-00,1012.0.10
508	6.02.9 62-1200 Existing SENT LFG		29-Jul-21 26-Sep-21 339 32-1500: FS, 12-1300: FS, 23-2200: FS	63-3000: FS, 63-4500: FS, M12. 4: FS -30, M12. 5: FS
507	6.02.9 62-1100 Existing SENT LTP	60	29-Jul-21 26-Sep-21 339 32-1500: FS, 12-1300: FS, 23-2200: FS	63-3000: FS, 63-4500: FS, M12. 4: FS -30, M12. 5: FS
506	6.02.9 62-1000 Existing SENT General Infrastructure Facility & Building	60	09-Jul-21 06-Sep-21 239 32-2100: FS, 12-1300: FS	23-2000: SS -90, 63-2800: FS, 63-2900: FS, 63-3000: FS, 63-4300: FS, M12. 4: FS -30, M12. 5: FS
505	SA2.6.02.9 Demolition of SENT Infrastructure Area		09-Jul-21 26-Sep-21 339	
504	SA2.6.02 Advance Works	80	09-Jul-21 26-Sep-21 339	
503	SA2.6 Construction (Remaining Works)	1474	01-Apr-19 13-Apr-23 30	
502	5.08.S 58-1300 Establishment of Screen Planting	270	01-Apr-19* 26-Dec-19 529 58-1200: SS	32-1500: FS
j01	5.08.S 58-1200 Advance Screen Planting		01-Apr-19* 29-Jun-19 529 23-7900: FS, 31-1100: FS, 11-1500: FS	58-1300: SS, M 3. 2: FS
500	SA2.5.08.S Area S	270	01-Apr-19 26-Dec-19 529	
i99	5.08.N 58-1100 Establishment of Screen Planting	270	01-Apr-19* 26-Dec-19 529 58-1000: SS, 14-1800: FS	32-1500: FS
ð	5.08.N 58-1000 Advance Screen Planting	90	01-Apr-19* 29-Jun-19 529 23-7900: FS, 31-1100: FS, 11-1500: FS	14-1800: SS -60, 58-1100: SS, 68-1600: SS 30, M 3. 2: FS
97	SA2.5.08.N Area N		01-Apr-19 26-Dec-19 529	
196	SA2.5.08 Landscape Works - Advance Screen Planting in CWB Country Park		01-Apr-19 26-Dec-19 529	
495	5.04.E 54-4700 Guard House & Entrance Gate	100	26-Jan-20 04-May-20 63 23-1300: FS, 23-5200: FS, 11-1100: FS, 11-1200: FS, 54-4500: SS 30	32-2100: FS, M 8. 2: FS, 12-1000: FS
			12-1000: FF, 11-1100: FS, 11-1200: FS	
494	5.04.E 54-4600 General Area & Access Road		09-Mar-20 06-Jul-20 6 53-5500: SS, 53-5600: FF, 53-6200: SS, 53-6300: FF,	32-2100: FS, 53-4900: FS, 53-5000: FS, 53-7000: FS
493	SA2.5.04.E Part X1 Area E & Part X2	163	26-Jan-20 06-Jul-20 6	
92	5.04.D 54-4500 Wheel Wash Bath	75	27-Dec-19 10-Mar-20 63 23-1300: FS, 23-5200: FS, 41-4500: FS, 11-1100: FS, 54-4200: SS 60	32-2100: FS, M 8. 3: FS, 12-1000: FS, 54-4700: SS 30
191	5.04.D 54-4400 Weighmaster House	120	29-Jun-19 26-Oct-19 64 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-2000: FS	32-2100: FS, M 8. 1: FS, 12-1000: FS, 54-4300: SS 60
190	5.04.D 54-4300 Weighbridge	75	29-Aug-19 11-Nov-19 63 41-4200: FS, 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-4400: SS 60	32-2100: FS, M 8. 6: FS -40, M 8. 7: FS, 54-4200: SS 60
89	5.04.D 54-4200 VWF Building	120	28-Oct-19 24-Feb-20 63 23-1300: FS, 23-5200: FS, 41-4500: FS, 11-1100: FS, 54-4300: SS 60	32-2100: FS, M 8. 4: FS, M 8. 6: FS -60, M 8. 7: FS, 12-1000: FS, 54-4500: SS 60
			53-6300: FF, 12-1000: FF, 11-1100: FS	53-7000: FS, M 8. 5: FS
488	5.04.D 54-4100 General Area & Access Road		09-Mar-20 06-Jul-20 6 23-1300: FS, 53-5500: SS, 53-5600: FF, 53-6200: SS,	32-2100: FS, 53-4800: FS, 53-4900: FS, 53-5000: FS,
487	SA2.5.04.D Part X1 Area D	37/	29-Jun-19 06-Jul-20 6	

# WBS Path Activity Activity Name	Dur Start Finish Total Predecessor Details	Successor Details		2018		20	110		21	120		2021			2022	2		2023
	Float		Q2	Q3	Q4 Q1	Q2	Q3	Q4 Q1	1 Q2	Q3	Q4 Q1	Q2	Q3 Q4	Q1	Q2	Q3	Q4	Q1 Q2 G
509 SA2.6.03 Civil Engineering Works	1259 02-Nov-19 13-Apr-23 30																	
510         SA2.6.03.2         Landfill Cell 2           511         6.03.2         63-1000         Earth bund (Eastern)	449         02-Nov-19         23-Jan-21         810           110         02-Nov-19         19-Feb-20         9         11-1100: FS, 23-2500: FS, 53-4200: FS, 53-1400: FS, 53-1400	53-3500; FS. 63-1500; FS. 63-1800; FS. 63-1900; FS.																
	53-2800: FS	63-2000: FS, 63-2100: FS, 63-2200: FS, M12. 1: FS -50, M12.																
		2: FS, 63-1100: FS																
512 6.03.2 63-1100 Earth bund (Western)	110 20-Feb-20 08-Jun-20 84 11-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: FS,	63-1400; FS. 63-1500; FS. 63-1700; FS. 63-3500; FS.																
	63-1000: FS	63-3600: FS, 63-1200: FS																
513 6.03.2 63-1200 Intercell bund (Cell 2/3)	90 09-Jun-20 06-Sep-20 734 11-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: FS,	63-1500: FS																
	53-4400: FS, 63-1100: FS																	
<b>514</b> 6.03.2 63-1300 Site Formation	75 02-Nov-19 15-Jan-20 14 11-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: FS	63-1400: FS, 63-4200: FS																
515 6.03.2 63-1400 Pump Station (PS#2X)	45 09-Jun-20 23-Jul-20 84 63-1300: FS, 63-1100: FS	63-1600: FS, 63-1700: FS																
516 6.03.2 63-1500 Lining Works	90 01-Oct-20* 29-Dec-20 710 41-1500: FS, 63-1000: FS, 63-1100: FS, 63-1200: FS	63-1600: FS, M12. 3: FS, 63-2400: FS												· · · · · · · · · · · · · · · · · · ·				
517 6.03.2 63-1600 Protective Stone Laying & Leachate Collection Pipe	25 30-Dec-20 23-Jan-21 810 63-1500: FS, 41-1500: FS, 63-1400: FS	32-1600: FS, M12. 3: FS																
518 6.03.2 63-1700 Install Leachate Force Main	75 24-Jul-20 06-Oct-20 84 63-1100: FS, 41-1500: FS, 63-1400: FS	54-2800: FS, M12. 3: FS																
519 6.03.2 63-1800 Install Landfill Gas Pipe on earth bund	35 20-Feb-20 25-Mar-20 168 41-1500: FS, 63-1000: FS	54-4000: FS, M12. 3: FS																
520 SA2.6.03.3 Landfill Cell 3	714 20-Feb-20 02-Feb-22 435																	
<b>521</b> 6.03.3 63-1900 Earth bund (Eastern)	110 20-Feb-20 08-Jun-20 9 11-1100: FS, 53-4200: FS, 63-1000: FS, 53-4300: FS, 53-2800: FS, 63-4200: FS	53-3300: FS, 53-3600: FS, 63-2400: FS, 63-2700: FS, M12. 1: FS -50, M12. 2: FS, 63-2000: FS -45, 63-2200: FS																
	55-2000. FS, 05-4200. FS	F3 -30, M12. 2. F3, 03-2000. F3 -43, 03-2200. F3																
522 6.03.3 63-2000 Earth bund (Western)	110 25-Apr-20 12-Aug-20 19 11-1100: FS, 63-1000: FS, 63-1900: FS -45	63-2300: FS, 63-2400: FS, 63-2600: FS, 63-3700: FS,																
		63-2100: FS -45																
523 6.03.3 63-2100 Intercell bund (Cell 3/4)	105         29-Jun-20         11-Oct-20         789         11-1100: FS, 63-1000: FS, 63-4200: FS, 63-2000: FS -45	63-2400: FS																
524 6.03.3 63-2200 Site Formation	75 09-Jun-20 22-Aug-20 9 11-1100: FS, 63-1000: FS, 63-1900: FS	63-2300: FS																
<b>525</b> 6.03.3 63-2300 Pump Station (PS#3X)	45 23-Aug-20 06-Oct-20 9 63-2200: FS, 63-2000: FS	63-2500: FS, 63-2600: FS																
<b>526</b> 6.03.3 63-2400 Lining Works	100 01-Oct-21* 08-Jan-22 435 41-1500: FS, 63-2000: FS, 63-2100: FS,	63-2500: FS, M12. 3: FS																
	63-1500: FS																	
527         6.03.3         63-2500         Protective Stone Laying & Leachate Collection Pipe	25 09-Jan-22 02-Feb-22 435 63-2400: FS, 41-1500: FS, 63-2300: FS	32-1700: FS, M12. 3: FS																
528 6.03.3 63-2600 Install Leachate Force Main	75 07-Oct-20 20-Dec-20 9 63-2000: FS, 41-1500: FS, 63-2300: FS	53-2500: SS -90, 54-2800: FS, M12. 3: FS																
529 6.03.3 63-2700 Install Landfill Gas Pipe on earth bund	35 09-Jun-20 13-Jul-20 58 41-1500: FS, 63-1900: FS	54-4000: FS, M12. 3: FS																
530 SA2.6.03.4 Landfill Cell 4	584 07-Sep-21 13-Apr-23 30																	
531 6.03.4 63-2800 Remaining Portion of Buttress Wall	120 07-Sep-21 04-Jan-22 494 62-1000: FS																	
532 6.03.4 63-2900 Earth bund (Western) incl. MSE Wall	120 07-Sep-21 04-Jan-22 239 62-1000: FS	63-3000: FS, 63-3100: FS, 63-3200: FS, 63-3400: FS,																
		63-3800: FS, 63-3900: FS, 63-4100: SS -90, M 9. 6: FS -60, M 9. 7: FS -30, M 9. 8: FS																
533 6.03.4 63-3000 Site Formation	120 05-Jan-22 04-May-22 239 62-1000: FS, 62-1200: FS, 63-2900: FS,	63-3100: FS																
	63-4100: FS	63-3300: FS, 63-3400: FS																
<b>534</b> 6.03.4 63-3100 Pump Station (PS#4X)	45 05-May-22 18-Jun-22 239 63-3000: FS, 63-2900: FS																	
535 6.03.4 63-3200 Lining Works	135 01-Oct-22* 12-Feb-23 0 41-1500: FS, 63-2900: FS	63-3300: FS, M12. 6: FS																<b></b>
536 6.03.4 63-3300 Protective Stone Laying & Leachate Collection Pipe	60         13-Feb-23         13-Apr-23         0         41-1500: FS, 63-3200: FS, 63-3100: FS	12-1900: FS, 32-1800: FS, M12. 6: FS																
537 6.03.4 63-3400 Install Leachate Force Main & Remove Temporary Leachate Pipe	30 19-Jun-22 18-Jul-22 269 41-1500: FS, 63-2900: FS, 63-3100: FS	12-1900: FS, 32-1800: FS, M12. 6: FS																
538         SA2.6.03.5         Drainage - Surface Run-Off           539         6.03.5         63-3500         Perimeter Channel (X9A) at Cell 2 Western Bund	750         16-Jan-20         03-Feb-22         464           15         09-Jun-20         23-Jun-20         1054         63-1100: FS	12-1900: FS																
540     6.03.5     63-3600     Perimeter Channel (X10A) at Cell 2 Western Bund		63-4000: FS																
	30         09-Jun-20         08-Jul-20         1029         63-1100: FS           20         42.0-x         20         44.0-x         20         62.0000         FC																	
541 6.03.5 63-3700 Perimeter Channel (X10A) at Cell 3 Western Bund	30         13-Aug-20         11-Sep-20         964         63-2000: FS	63-4000: FS																
542 6.03.5 63-3800 Perimeter Channel (X10A) at Cell 4 Western Bund	20 05-Jan-22 24-Jan-22 464 63-2900: FS	63-4000: FS																
543 6.03.5 63-3900 Perimeter Channel (X10C) at Cell 4 Western Bund	15 05-Jan-22 19-Jan-22 469 63-2900: FS	63-4000: FS																
544 6.03.5 63-4000 Connection to Existing DP3	10 25-Jan-22 03-Feb-22 464 63-3900: FS, 63-3600: FS, 63-3700: FS, 63-3800: FS	12-1900: FS																
545 6.03.5 63-4100 Remove Cut-Off Channel C-7 at bottom of Buttress Wall	30 09-Jun-21 08-Jul-21 419 63-2900: SS -90	63-3000: FS																
546 6.03.5 63-4200 Temporary Channel (X7T) at SENT Infrastructure Area	30 16-Jan-20 14-Feb-20 14 63-1300: FS	63-1900: FS, 63-2100: FS																
547 SA2.6.03.6 Drainage - Ground Water	85 07-Sep-21 30-Nov-21 529																	
548         6.03.6         63-4300         Construct Temporary Channel (TC-1), from MH-1 to Existing UC-825	50         07-Sep-21         26-Oct-21         529         23-1900: FS, 11-1300: FS, 62-1000: FS	63-4400: FS																
549 6.03.6 63-4400 Divert GW at MH-1 to TC-1	5 27-Oct-21 31-Oct-21 529 63-4300: FS	63-4500: FS, M 9. 9: FS																
550 6.03.6 63-4500 Reconnection of GWCP across Cell 4	30 01-Nov-21 30-Nov-21 529 62-1100: FS, 62-1200: FS, 63-4400: FS	12-1900: FS																
551 SA2.6.03.8 Utilities - Works Associated with Utilities Undertakers	255 15-Nov-20 27-Jul-21 655																	
552 SA2.6.03.8.U1 CLP	210 30-Dec-20 27-Jul-21 655																	
553 6.03.8.U1 63-4600 LFG Generator On-grid Testing	180         30-Dec-20         27-Jun-21         655         32-2500: FS, 12-1200: FS, 54-4000: FS	63-4700: FS																
554 6.03.8.U1 63-4700 LFG Generator On-grid Inspection & Verify	30 28-Jun-21 27-Jul-21 655 63-4600: FS	12-1900: FS																
555 <u>SA2.6.03.8.U6 TownGas</u>	55 15-Nov-20 08-Jan-21 855													·····				
556 6.03.8.U6 63-4800 Laying Gas Mains (from LFG to Town Gas PF)	45 15-Nov-20 29-Dec-20 855 54-4000: FF	63-4900: FS																
557 6.03.8.U6 63-4900 Gas Meter Relocation & Connection at LFG	10 30-Dec-20 08-Jan-21 855 63-4800: FS, 54-4000: FS	12-1900: FS																
558 SA2.6.04 Building & E&M Works	661 01-Oct-19 22-Jul-21 660																	
559         SA2.6.04.C Part X1 Area C           560         SA2.6.04.C.02 LFG Treatment Plant	661         01-Oct-19         22-Jul-21         660           661         01-Oct-19         22-Jul-21         660																	
561         6.04.C.02         64-1000         GHS600 Blower 601 C Relocation	15 08-Jul-21 22-Jul-21 660 32-1500: FS	12-1900: FS																
562 6.04.C.02 64-1100 Absorption Chiller (Optional)	90 01-Oct-19 29-Dec-19 1231 54-2200: FS	12-1900: FS																
563 SA2.6.08 Landscape Works	613 01-Apr-19 03-Dec-20 891																	
564 SA2.6.08.1 SENT Area - Tree Removal & Transplanting	240 01-Apr-19 26-Nov-19 1264																	
565         6.08.1         68-1000         Access trees condition and select for transplanting	30 01-Apr-19* 30-Apr-19 1264 14-1300: FS	68-1100: FS, 68-1200: FS, 68-1400: FS																
566         6.08.1         68-1100         Prepare new site to receive trees	90 01-May-19 29-Jul-19 1264 68-1000: FS	68-1200: SS																
567 6.08.1 68-1200 Transplant selected trees	120 01-May-19 28-Aug-19 1264 68-1000: FS, 68-1100: SS	68-1300: FS																
568 6.08.1 68-1300 Prune trees prior to removal from Cell 4	90 29-Aug-19 26-Nov-19 1264 68-1200: FS	12-1900: FS																
569 6.08.1 68-1400 Tree Felling - Part X3	90 01-May-19 29-Jul-19 1384 23-8200: FS, 31-1600: FS, 68-1000: FS	12-1900: FS																
570 SA2.6.08.2 SENTX Area - Trial Nursery & Tree Planting	583 01-May-19 03-Dec-20 891																	
571         6.08.2         68-1600         Trial Nursery	300 01-May-19 24-Feb-20 1174 14-1800: FS, 58-1000: SS 30	12-1900: FS, M 3. 2: FS					·····	+										
572 6.08.2 68-1700 Landscaping in New Infrastructure Area	150 07-Jul-20 03-Dec-20 891 54-1000: FS, 23-7600: FS	12-1900: FS																

Remaining Work		South-East New Territories Land Fill Extension (SA2-SENTX)	Date	Revision	Checked	Approved
	Page : 4 of 4		11-May-18	SENTX-GVL-W-PB-ZZ-0001 Rev. I01		
<ul> <li>Milestone</li> </ul>		Baseline Programme	20-Jul-18	SENTX-GVL-W-PB-ZZ-0001 Rev. I02 (Detailed)		

Annex B

### Environmental Mitigation Implementation Schedule

### Annex B Environmental Mitigation Implementation Schedule

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the		<b>implement</b> ure? <sup>(1)</sup> O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
Air Quali	ty – Cons	truction Phase								
4.8.1	AQ1	<ul> <li><u>Blasting</u></li> <li>The area within 30m of the blasting area will be wetted prior to blasting.</li> </ul>	To minimise potential dust nuisance	Blasting area and 30m of blasting area	SENTX Contractor		✓		Air Pollution Control (Construction Dust) Regulations	Not applicable. Blasting is not required in the latest landfill design
		• Blasting will not be carried out when the strong wind signal or tropical cyclone warning signal No. 3 or higher is hoisted, unless this is with the express prior permission of the Commissioner of Mines.								uesign
		• loose material and stones in the Site will be removed prior to the blast operation								
		• During blasting, blast nets, screens and other protective covers will be used to prevent the projection of flying fragments and material resulting from blasting								
4.8.1	AQ2	<ul> <li><u>Rock Drilling</u></li> <li>Watering will be carried out at the rock drilling activities to avoid fugitive dust emissions.</li> </ul>	To minimise potential dust nuisance	Rock drilling area	SENTX Contractor		✓		Air Pollution Control (Construction Dust) Regulations	Not applicable. Rock drilling is not required in the latest landfill design
4.8.1	AQ3	Site Access Road	To minimise	Main haul	SENTX		✓		Air Pollution Control	Implemented

(1) D=Design; C=Construction; O/R=Operation/Restoration; A=Aftercare

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the me	to impleme asure? <sup>(1)</sup> O/R 2	or standards for the	Implementation Status and Remarks
		• The main haul road will be kept clear of dusty materials or sprayed with water.	potential dust nuisance	road	Contractor			(Construction Dust) Regulations	
		• The main haul road will be paved with aggregate or gravel.						HKAQO and EIAO- TM Annex 4	
		• Vehicle speed will be limited to 10kph.							
4.8.1	AQ4	Stockpiling of Dusty Materials	To minimise	All	SENTX	$\checkmark$		Air Pollution Control	Deficiency of
		• Any stockpile of dusty materials will be covered entirely by impervious sheeting	potential dust nuisance	construction works area	Contractor			(Construction Dust) Regulations	mitigation measures but rectified by the Contractor
		or placed in an area sheltered on the top and three sides or sprayed with water so as to ensure that the entire surface is wet.						HKAQO and EIAO- TM Annex 4	
4.8.1	AQ5	Loading, unloading or transfer of dusty_ materials	To minimise potential dust	All construction	SENTX Contractor	~		Air Pollution Control (Construction Dust)	Reminder was given to the Contractor
		• All dusty materials will be sprayed with	nuisance	works area				Regulations	
		water immediately prior to any loading, unloading or transfer operation so as to maintain the dusty material wet.						HKAQO and EIAO- TM Annex 4	
4.8.1	AQ6	Site Boundary and Entrance	To minimise	Site boundary	SENTX	$\checkmark$		Air Pollution Control	Not applicable
		• Where a site boundary adjoins a road, street, service lane or other area accessible	potential dust nuisance	and entrance	Contractor			(Construction Dust) Regulations	
		to the public, hoarding of height not less than 2.4m from ground level will be provided along the entire length of that portion of the site boundary except for the site entrance or exit.						HKAQO and EIAO- TM Annex 4	
4.8.1	AQ7	Excavation Works	To minimise	All	SENTX	$\checkmark$		Air Pollution Control	Deficiency of

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? <sup>(1)</sup> D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		• Working area of any excavation or earth moving operation will be sprayed with water immediately before, during and immediately after the operation so as to ensure that the entire surface is wet.	potential dust nuisance	construction works area	Contractor		(Construction Dust) Regulations HKAQO and EIAO- TM Annex 4	mitigation measures but rectified by the Contractor
4.8.1	AQ8	<ul> <li>Building Demolition</li> <li>The area where the demolition works are planned to take place will be sprayed with water immediately prior to, during and immediately after the demolition activities.</li> <li>Any dusty materials remaining after a stockpile is removed will be wetted with water and cleared from the surface of</li> </ul>	To minimise potential dust nuisance	All construction works area	SENTX Contractor	✓	Air Pollution Control (Construction Dust) Regulations HKAQO and EIAO- TM Annex 4	Implemented
4.8.1	AQ9	<ul> <li>roads or street.</li> <li><u>Construction of the Superstructure of</u> <u>Building</u></li> <li>Effective dust screens, sheeting or netting will be provided to enclose the scaffolding from the ground level up to the highest level of the scaffolding.</li> </ul>	To minimise potential dust nuisance	All construction works area	SENTX Contractor	✓	Air Pollution Control (Construction Dust) Regulations HKAQO and EIAO- TM Annex 4	Implemented
4.8.1	AQ10	Should a stone crushing plant be needed on site, the control measures recommended in the <i>Best Practicable Means Requirement for</i> <i>Mineral Works (Stone Crushing Plants) BPM</i> 11/1 should be implemented.	To minimise potential dust nuisance	Stone crushing plant/ construction phase	SENTX Contractor	✓	Best Practicable Means Requirement for Mineral Works (Stone Crushing Plants) BPM 11/1	Not applicable. Stone crushing plant is not required in the latest landfill design

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main	Location of the Measures	Who to implement the measure?			implement sure? <sup>(1)</sup> O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
			Concerns to address				-	- /		
4.8.1	AQ11	Good site practices such as regular maintenance and checking of the diesel powered mechanical equipment will be adopted to avoid any black smoke emissions and to minimize gaseous emissions.	To minimise potential dust nuisance	All construction works area	SENTX Contractor		~		HKAQO and EIAO- TM Annex 4	Implemented
4.10.1	AQ12	Dust monitoring once every 6 days	Ensure the dust generated from the project meets the air quality requirement	At monitoring locations shown in <i>Figure 3.2a</i>	SENTX Contractor		•		HKAQO and EIAO- TM Annex 4	Implemented
Air Quali	ty - Oper	ation, Restoration and Aftercare Phases								
4.8.2	AQ13	Odour • Enclosing the weighbridge area	To minimise odour nuisance	Weighbridge area	SENTX Contractor	✓		~	EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only which is significantly less odorous, enclosing the weighbridge area is not necessary
4.8.2	AQ14	• Providing a vehicle washing facility before the exit of SENTX and providing sufficient signage to remind RCV drivers to pass through the facility before leaving SENTX		Vehicle washing facility	SENTX Contractor	✓		✓	EIAO-TM Annex 4	Implemented
4.8.2	AQ15	• Reminding the RCV drivers to empty the liquor collection sump and close the valve	To minimise odour nuisance	Tipping face	SENTX Contractor			✓	EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement	When to the mea	sure? (1)		What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address		the measure?	D C	O/R	А	measure to achieve?	
		before leaving the tipping face								only, which is relatively dry, the amount of liquor generated is expected to minimal
4.8.2	AQ16	• Washing down the area where spillage of RCV liquor is discovered promptly	To minimise odour nuisance	SENTX Site	SENTX Contractor		~		EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only, which is relatively dry, the amount of liquor generated is expected to minimal.
4.8.2	AQ17	• Reminding operators to properly maintain their RCVs and ensure that liquor does not leak from the vehicles		SENTX Site	SENTX Contractor		V		EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only, which is relatively dry, the amount of liquor generated is expected to minimal.
4.8.2	AQ18	• Installation of landfill gas control system to enhance collection of landfill gas from the waste mass and hence minimise odour associated with fugitive landfill gas emissions	To minimise odour nuisance	SENTX Site	SENTX Contractor	✓	✓	✓	EIAO-TM Annex 4	Implemented
4.8.2	AQ19	• Progressive restoration of the areas which	To minimise	SENTX Site	SENTX	✓	√	✓	EIAO-TM Annex 4	Implemented

EIA Ref.	EM&A Ref		nvironmental Protection Measures/ Aitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement			impler ure? <sup>(1)</sup>	nent	What requirements or standards for the	Implementation Status and Remarks
	Kei	10	ningation weasures	Measure & Main Concerns to address	the measures	the measure?		C	O/R	А	measure to achieve?	Status and Kentarks
			reach the finished profile (a final capping system including an impermeable liner will be put in place) and installation of a permanent landfill gas extraction system	odour nuisance		Contractor						
4.8.2	AQ20	•	Installing deodorizers along the site boundary adjacent to the ASRs	To minimise odour nuisance	SENTX Site boundary	SENTX Contractor			*	•	EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only which is significantly less odorous, installation of deodorizers is not necessary.
4.8.2	AQ21	•	Erecting a vertical barrier, wall or structure softened by planting rows of trees/shrubs or landscape feature along the site boundary, particularly in the areas near the ASRs		SENTX Site boundary	SENTX Contractor	~		✓	~	EIAO-TM Annex 4	Implemented
4.8.2 and SENTX latest design	AQ22	•	Maintaining the size of the active tipping face not greater than 1,200 m <sup>2</sup>	To minimise odour nuisance	Active tipping face	SENTX Contractor			~		EIAO-TM Annex 4	Implemented
4.8.2	AQ23	•	Promptly covering the MSW with soil or selected inert materials to control odour emissions	To minimise odour nuisance	Active tipping face	SENTX Contractor			✓		EIAO-TM Annex 4	Not Applicable. SENTX will not receive MSW.
4.8.2	AQ24	•	Maintaining the size of the special waste trench not greater than $6m (l) \times 2.5m (w)$	To minimise odour nuisance	Special waste trench	SENTX Contractor			✓		EIAO-TM Annex 4	Not Applicable. SENTX will not have

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? <sup>(1)</sup> D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
								any special waste trench.
4.8.2 and SENTX latest design	AQ25	• Covering daily covered area with a tarpaulin sheet or 300mm of soil after the landfill operating hours	To minimise odour nuisance	Daily covered area	SENTX Contractor	✓	EIAO-TM Annex 4	Implemented
4.8.2	AQ26	• Covering special waste trench with 600 mm of soil and an impervious liner after 5 pm	To minimise odour nuisance	Special waste trench	SENTX Contractor	$\checkmark$	EIAO-TM Annex 4	Not Applicable. SENTX will not have any special waste trench.
4.8.2	AQ27	• Covering the non-active tipping face with 600mm of soil and an impermeable liner (on top of the intermediate cover), which will not only control odour emissions from landfilled waste but also enhance landfill gas extraction by the landfill gas extraction system		Intermediate cover	SENTX Contractor	✓	EIAO-TM Annex 4	Implemented
4.8.2	AQ28	• Applying deodorizers or odour suppression agents to control odour emissions from the active tipping face and special waste trench, if any, through spraying or fogging equipment	To minimise odour nuisance	Active tipping face and special waste trench	SENTX Contractor	✓	EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only which is significantly less odorous, installation of deodorizers is not necessary. Moreover, SENTX will not have any special waste

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to the mea D C		)	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
4.8.2	AQ29	• Providing a mobile cover with retractable or suitable opening to cover up the opening of the special waste trench except during waste deposition and a suitable odour removal unit. The mobile cover should be equipped with powered extraction and suitable odour removal unit for purifying the trapped gas inside the trench before release into the atmosphere	To minimise odour nuisance	Special waste trench	SENTX Contractor		✓		EIAO-TM Annex 4	trench. Not Applicable. SENTX will not have any special waste trench.
4.8.2 and SENTX latest design	AQ30	• Providing a thermal oxidizer for the leachate treatment plant	To minimise odour nuisance as a result of breakdown of thermal oxidizer	Leachate treatment plant	SENTX Contractor	✓	✓	~	EIAO-TM Annex 4	Implemented
4.8.2 and SENTX latest design	AQ31	• Enclosing all the leachate storage and treatment tanks (except for the Sequential Batch Reactor (SBR) or Membrane Bioreactor (MBR) tanks) and diverting the exhaust air from these tanks to a thermal oxidizer or flare to avoid potential odour emissions from the LTP	To minimise odour nuisance	Leachate treatment plant	SENTX Contractor	✓	✓	~	EIAO-TM Annex 4	Implemented
4.8.2	AQ32	• Rescheduling of waste filling activities on- site by avoiding waste filling activities carrying out at the northern area of the site in the summer months between July to November	To minimise odour nuisance	SENTX Site	SENTX Contractor		✓		EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only which is significantly less

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	the Measures	Who to implement	When the m		mplen re? <sup>(1)</sup>	nent	What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address		the measure?	D	С	O/R	А	measure to achieve?	
											odorous, rescheduling of waste filling activities is not necessary.
4.8.2 and SENTX latest design	AQ33	<ul> <li><u>Dust, Gaseous Emission and LFG including</u></li> <li><u>Volatile Organic Compounds (VOCs)</u></li> <li>Keeping the main haul road to the waste filling area wet by regular watering ;</li> </ul>	To minimise dust nuisance	SENTX Site	SENTX Contractor			✓		HKAQO and EIAO- TM Annex 4	Implemented
4.8.2	AQ34	• Compacting the exposed daily and intermediate covered areas well to avoid fugitive dust emission;	To minimise dust nuisance	SENTX Site	SENTX Contractor			✓		HKAQO and EIAO- TM Annex 4	Implemented
4.8.2	AQ35	• Limiting the vehicle speed within SENTX site boundary;	To minimise dust nuisance	SENTX Site	SENTX Contractor			√		HKAQO and EIAO- TM Annex 4	Implemented
4.8.2	AQ36	<ul> <li>Providing vehicle washing bay to avoid vehicles carrying dust to public roads;</li> </ul>	To minimise dust nuisance	SENTX Site	SENTX Contractor			√		HKAQO and EIAO- TM Annex 4	Implemented
4.8.2	AQ37	• Switching off the engine when the diesel- driven equipment is idling;	To minimise gaseous emissions	SENTX Site	SENTX Contractor			✓	✓	-	Implemented
4.8.2	AQ38	<ul> <li>Maintaining the construction equipment properly to avoid any black smoke emissions;</li> </ul>	To minimise gaseous emissions	SENTX Site	SENTX Contractor			✓	✓	-	Implemented
4.8.2	AQ39	Providing sufficient underground landfill gas collection system to capture the landfill gas	To minimise gaseous	SENTX Site	SENTX Contractor			√	✓	EIAO-TM Annex 4	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended		Who to implement			implei ure? <sup>(1)</sup>		What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address		the measure?	D	С	O/R	А	measure to achieve?	
		generated as much as possible; and	emissions, including LFG and VOCs								
4.8.2	AQ40	Periodic inspections of the final cover should be undertaken to ensure that the capping layer is in good conditions at all times.	To minimise gaseous emissions, including LFG and VOCs	SENTX Site	SENTX Contractor			✓	✓	EIAO-TM Annex 4	Implemented
4.10.2	AQ41	Monitoring of ambient TSP once every 6 days	Ensure the dust emission from the project meets the dust requirement	shown in	SENTX Contractor		✓	~		HKAQO and EIAO- TM Annex 4	Implemented
4.10.2	AQ42	Monitoring of ambient VOCs, ammonia and H <sub>2</sub> S, quarterly	Ensure the gaseous emission from the project meets the air quality requirement	At monitoring locations shown in <i>Figure 11.3a</i>	SENTX Contractor			~	✓	Odour thresholds or 1% of Occupational Exposure Limit (OEL) as stipulated in the "UK Health and Safety Executive (HSE) EH 40/05 Occupational Exposure Limits", whichever is lower.	Implemented
4.10.2 and SENTX latest	AQ43	Monitoring of parameters for thermal oxidizer, flares and generator in accordance with requirements stated in Tables 3.4a, 3.5a and 3.6a of the EM&A Manual respectively.	Ensure the gaseous emission from the project meets the air	At the flares and thermal oxidizer stacks when they are	SENTX Contractor			✓	<ul><li>✓</li><li>(1)</li></ul>	Emission Limits specified in Contract	Implemented

(1) For LFG flare and LFG generator only.

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the r	neas	implen ure? <sup>(1)</sup> O/R		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
design			quality requirement	in operation							
4.10.2	AQ44	To confirm design assumption of ammonia, it is recommended that the ammonia concentration in the flue gas of the thermal oxidiser be monitored during the commissioning stage of the thermal oxidiser. If required, an emission standard will be set for ammonia for the thermal oxidiser based on the monitoring results. If no ammonia is detected in the flue gas during the decommissioning stage, the monitoring of ammonia in the flue gas of the thermal oxidiser could be discontinued.	Ensure the gaseous emission from the project meets the air quality requirement	At the thermal oxidizer stack during commissioning . If ammonia is detected during commissioning stage, the monitoring will continue.	SENTX Contractor			•		Emission Limits determined during commissioning stage	Implemented
4.10.2 and SENTX latest design	AQ45	Odour patrol in accordance with requirements stated in Table 3.7a of the EM&A Manual.	Ensure the odour emission from the project meets the odour requirement	U U	SENTX Contractor			✓		EIAO-TM Annex 4	Implemented
4.10.2	AQ46	Monitoring of meteorological station, continuously	Collect site specific meteorological data	At meteorological station shown in <i>Figure 11.3a</i>	SENTX Contractor		✓	✓	✓	-	Implemented
Noise – C	onstructio	on Phase									
5.7.1	N1	<ul><li>Adopt good site practice listed below:</li><li>Only well-maintained plant will be</li></ul>	To minimise potential construction	All construction	SENTX Contractor		✓			Noise Control Ordinance (NCO) and	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the mea	o implement sure? <sup>(1)</sup> O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		operated on-site and plant should be serviced regularly during the construction program;	noise nuisance.	works area				EIAO-TM Annex 5	
		• Silencers or mufflers on construction equipment should be utilized and will be properly maintained during the construction program;							
		• Mobile plant, if any, will be sited as far from NSRs as possible;							
		• Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or should be throttled down to a minimum;							
		• Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and							
		• Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.							
5.8	N2	Weekly noise monitoring	Ensure noise generated from the project meets the criteria	At monitoring locations shown in <i>Figure 6.4a</i>	SENTX Contractor	~		Noise Control Ordinance (NCO) and EIAO-TM Annex 5	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the r		implem ure? <sup>(1)</sup> O/R	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
Noise – O	peration/	Restoration Phase								
5.7.2	N3	<ul><li>Adopt good site practice listed below:</li><li>Choose quieter PME;</li></ul>	To minimise potential operational noise nuisance.	Within the SENTX Site	SENTX Contractor			✓	Noise Control Ordinance (NCO) and EIAO-TM Annex 5	Implemented
		<ul> <li>Include noise levels specification when ordering new plant items;</li> </ul>							-	Implemented
		• Locate fixed plant items or noise emission points away from the NSRs as far as practicable;							-	Implemented
		<ul> <li>Locate noisy machines in completely enclosed plant rooms or buildings; and</li> </ul>							-	Implemented
		• Develop and implement a regularly scheduled plant maintenance programme so that plant items are properly operated and serviced. The programme should be implemented by properly trained personnel.							-	Implemented
5.8	N4	Weekly noise monitoring	Ensure noise generated from the project meets the criteria	At monitoring locations shown in <i>Figure 6.4a</i>	SENTX Contractor			✓	Noise Control Ordinance (NCO) and EIAO-TM Annex 5	Implemented
Water Qu	ality - Co	onstruction Phase								
6.8.1	WQ1	Construction Runoff								
		• Exposed soil areas will be minimised to	To minimise	All	SENTX		✓		ProPECC PN 1/94	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main	Location of the Measures	Who to implement the measure?	the		o implement sure? <sup>(1)</sup> O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
			Concerns to address							
		reduce the contamination of runoff and erosion.	potential water quality impacts arising from the construction works	construction works area	Contractor				EIAO-TM Annex 6	
6.8.1	WQ2	• Perimeter channels will be constructed in	To minimise	All	SENTX	$\checkmark$	$\checkmark$		ProPECC PN 1/94	Reminder was given to
		advance of site formation works and earthworks and intercepting channels will be provided for example along the edge of	potential water quality impacts arising from the	construction works area	Contractor				Water Pollution Control Ordinance (WPCO)	the Contractor
		excavation.	construction works						EIAO-TM Annex 6	
6.8.1	WQ3 •	<ul> <li>Silt removal facilities, channels and manholes will be maintained and the deposited silt and grit should be removed</li> </ul>	To minimise	All construction works area	SENTX		$\checkmark$		ProPECC PN 1/94	Deficiency of
			potential water quality impacts		Contractor				WPCO	mitigation measures but rectified by the
		regularly to ensure they are functioning properly at all times.	arising from the construction works	works area					EIAO-TM Annex 6	Contractor
6.8.1	WQ4	• Temporary covers such as tarpaulin will	To minimise	All	SENTX		$\checkmark$		ProPECC PN 1/94	Implemented
		also be provided to minimise the generation of high SS runoff.	potential water quality impacts arising from the construction works	construction works area	Contractor				WPCO	
6.8.1	WQ5	• The surface runoff contained any oil and	To minimise	All	SENTX		$\checkmark$		ProPECC PN 1/94	Implemented
		grease will pass through the oil potential water construction interceptors. quality impacts works area	Contractor				WPCO			
			ors. quality impacts works area arising from the construction works					EIAO-TM Annex 6		

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the m	easu	mplement tre? <sup>(1)</sup> O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
6.8.1	WQ6	• All sewer and drains will be sealed to prevent building debris, soil etc from entering public sewers/drains before commencing any demolition works	To minimise potential water quality impacts arising from the demolition works	Infrastructure area at existing SENT Landfill	SENTX Contractor	`	~		ProPECC PN 1/94 WPCO EIAO-TM Annex 6	Not applicable
6.8.1	WQ7	• During the excavation works for the twin drainage tunnels, the recycle water for cooling the cutter head of the TBM will be conveyed to the sedimentation tanks for treatment and most of the treated water will be reused, where applicable and as much as possible, in the boring operations.	To minimise potential water quality impacts arising from the tunnel works	Tunnel boring sites	SENTX Contractor		~		ProPECC PN 1/94 WPCO EIAO-TM Annex 6	Not applicable. Excavation of drainage tunnels is not required in the latest landfill design.
6.8.1	WQ8	• The fuel and waste lubricant oil from the on-site maintenance of machinery and equipment will be collected by a licensed chemical waste collector.	To minimise potential water quality impacts arising from improper handling of fuel and oil	SENTX Site	SENTX Contractor	、	•		ProPECC PN 1/94 WPCO Waste Disposal Ordinance (WDO)	Implemented
6.8.1	WQ9	• Implementation of excavation schedules, lining and covering of excavated stockpiles	To minimise contaminated stormwater run- off from the SENTX Site	All construction works	SENTX Contractor	、	~		ProPECC PN 1/94 WPCO EIAO-TM Annex 6	Implemented
6.13	WQ10	• Monitoring of surface water quality will be conducted on a regular basis as stated in the EM&A Manual.	To minimise potential water quality impacts on surface water arising from the	SENTX Site	SENTX Contractor	•	~		WPCO Water-TM	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address construction works	Location of the Measures	Who to implement the measure?	the 1	meas	<b>implement</b> ure? <sup>(1)</sup> O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
6.8.2	WQ11	Sewage Effluents								
		• Sufficient chemical toilets will be provided for the construction workforce.	To minimise potential water quality impacts arising from the sewage effluents	SENTX Site	SENTX Contractor		~		WPCO	Implemented
6.8.2	WQ12	• Untreated sewage will not be allowed to	To minimise	SENTX Site	SENTX		✓		WPCO	Deficiency of
		discharge into the surrounding water body.	potential water quality impacts arising from the sewage effluents		Contractor				WDO	mitigation measures but rectified by the Contractor
6.8.2	WQ13	• A licensed waste collector will be	To minimise	SENTX Site	SENTX		✓		WPCO	Implemented
		employed to clean the chemical toilets on a regular basis.	potential water quality impacts arising from the sewage effluents		Contractor				WDO	
Water Qu	ality – O	peration/Restoration and Aftercare Phases								
6.9.1	WQ14	Surface Water Management							WPCO	Implemented
		• Inspections of the drainage system, sand traps, settlement ponds and surface water channels will be performed regularly to identify areas necessary for maintenance, cleaning or repair.	To minimise potential water quality impacts on surface water arising from the landfill operations.	SENTX Site	SENTX Contractor			~	Technical Memorandum Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Inshore Waters (Water- TM)	

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When the mo D (	easu	-		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
6.9.1	WQ15	• Regular maintenance and replacement, if required, of the HDPE liner will be conducted to prevent degradation from affecting the performance of the capping system.	To minimise potential water quality impacts on surface water arising from the landfill operations.	SENTX Site	SENTX Contractor			V		EIAO-TM Annex 6 WPCO Water-TM EIAO-TM Annex 6	Implemented
6.9.1	WQ16	• Monitoring of surface water quality will be conducted on a regular basis as stated in the EM&A Manual.	e To minimise potential water quality impacts on surface water arising from the landfill operations.	SENTX Site	SENTX Contractor			✓	•	WPCO Water-TM	Implemented
6.9.2 and SENTX latest design	WQ17	<ul> <li>Groundwater Management</li> <li>The groundwater management facilities including the groundwater monitoring wells will be inspected regularly during routine groundwater monitoring programme.</li> </ul>	To minimise potential water quality impacts on groundwater arising from the landfill operations.	SENTX Site	SENTX Contractor			✓	✓	WPCO Water-TM EIAO-TM Annex 6	Implemented
6.9.2	WQ18	• Monitoring of groundwater water quality will be conducted on a regular basis as stated in the EM&A Manual.	To minimise potential water quality impacts on groundwater arising from the	SENTX Site	SENTX Contractor			✓	✓	WPCO Water-TM EIAO-TM Annex 6	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement		implen ure? <sup>(1)</sup>	nent	What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address landfill operations.		the measure?	C	O/R	A	measure to achieve?	
SENTX latest design	WQ19	<ul> <li>Sewage</li> <li>All sewage from the operation staff will be diverted to the LTP for treatment or public sewer, if available.</li> </ul>	To ensure proper handling of sewage	SENTX Site	SENTX Contractor		✓	✓	-	Implemented
6.9.3	WQ20	<ul> <li>Leachate Management</li> <li>The leachate pump houses and related ancillary equipment will be inspected regularly and repairs, if necessary.</li> </ul>	To minimise potential water quality impacts on surrounding water bodies arising from the landfill operations.	Leachate pump houses and related ancillary equipment	SENTX Contractor		✓	•	WPCO Water-TM EIAO-TM Annex 6	Implemented
6.9.3	WQ21	• For equipment such as pumps that require routine scheduled maintenance, the maintenance will be performed following manufacturer's recommended frequency.	To minimise potential water quality impacts on surrounding water bodies arising from the landfill operations.	Leachate pumps	SENTX Contractor		✓	•	WPCO Water-TM	Implemented
6.9.3	WQ22	• Preventive maintenance will be implemented so that the possibility for forced shutdown during wet season will be kept to minimal.	To minimise potential water quality impacts on surrounding water bodies	Leachate treatment plant	SENTX Contractor		✓	✓	WPCO Water-TM EIAO-TM Annex 6	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement	When the me		-	ent	What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address arising from the landfill operations.		the measure?			D/R	A	measure to achieve?	
6.9.3	WQ23	• Emergency procedures or a contingency plan will be established when the LTP is malfunctioned.	To minimise potential water quality impacts on surrounding water bodies arising from the landfill operations.	Leachate treatment plant	SENTX Contractor		v	/	•	WPCO Water-TM EIAO-TM Annex 6	Implemented
6.9.3 and SENTX latest design	WQ24	• There will be sufficient redundancy in the system to handle the leachate flow even if one treatment train is down for maintenance. The leachate may be required to temporarily store within the landfill if the leachate storage lagoon are full and leachate cannot be transported to the LTP for treatment.	To minimise potential water quality impacts on surrounding water bodies arising from the landfill operations.	Leachate treatment plant	SENTX Contractor		v	/	~	WPCO Water-TM EIAO-TM Annex 6	Implemented
6.13	WQ25	• Monitor the quality of effluent discharged from the LTP	To ensure discharge quality comply with WPCO requirement	Leachate treatment plant discharge point	SENTX Contractor		v	/	~	WPCO Water-TM	Implemented
6.10.1	WQ26	<ul> <li>Potential Leakage of Leachate</li> <li>Regular groundwater quality monitoring will be carried out to monitor the performance of the leachate containment system.</li> </ul>	To minimise potential water quality impacts on surrounding	SENTX Site	SENTX Contractor		v	/	✓	WPCO Water-TM	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement	the	meas	implen ure? <sup>(1)</sup>		What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address		the measure?	D	С	O/R	А	measure to achieve?	
			water bodies arising from the landfill operations.								
6.10.1	WQ27	Maintenance and replacement of the	To minimise	SENTX Site	SENTX			✓	✓	WPCO	Implemented
		capping system should be carried out, if necessary, to prevent control infiltration	potential water quality impacts		Contractor					Water-TM	
		and leachate seepage from any damaged cap.	on surrounding water bodies arising from the leachate leakage.							EIAO-TM Annex 6	
6.10.1	WQ28	• Maintaining control of the leachate level	To minimise	SENTX Site	SENTX			✓	✓	WPCO	Implemented
		through extraction	potential water quality impacts		Contractor					Water-TM	
			on surrounding water bodies arising from surface breakout of leachate.							EIAO-TM Annex 6	
Waste Ma	anagemen	t - Construction Phase									
7.6.1	WM1	All the necessary waste disposal permits are obtained prior to the commencement of construction work.	To ensure compliance with relevant statutory requirements	Before construction works commence	SENTX Contractor	✓	✓			WDO	Implemented
7.6.1	WM2	Management of Waste Disposal									
		The construction contractor will open a billing account with the EPD Every	To ensure that	SENTX Site	SENTX		✓			WDO	Implemented
		billing account with the EPD. Every construction waste or public fill load to be	adverse environmental		Contractor					Waste Disposal (Charges for Disposal	

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the mea	o implement sure? <sup>(1)</sup> O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		transferred to the Government waste disposal facilities such as public fill reception facilities,	*					of Construction Waste) Regulation;	
		sorting facilities, landfills will required a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste						Works Bureau Technical Circular No.31/2004; and	
		producer. A trip-ticket system will also be established to monitor the disposal of construction waste at the SENT Landfill and to control fly-tipping. The trip-ticket system will be included as one of the contractual requirements and implemented by the contractor.						Annex 5 and Annex 6 of Appendix G of ETWBTC No. 19/2005)	
		A recording system for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established.							
7.6.1	WM3	Measures for the Reduction of Construction Waste Generation							
		Inert and non-inert construction waste will be segregated and stored in different containers or skips to facilitate reuse or recycling of the inert waste and proper disposal of the non- inert construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	To reduce construction waste generation	SENTX Site	SENTX Contractor	×		WDO EIAO-TM Annex 7	Implemented
7.6.1	WM4	Chemical Waste							
						$\checkmark$		WDO	

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? <sup>(1)</sup> D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		The construction contractor will register as a chemical waste producer with the EPD. Chemical waste will be handled in accordance with the <i>Code of Practice on the Packaging, Handling and Storage of Chemical Wastes</i> .	To ensure proper handling of chemical waste	SENTX Site	SENTX Contractor		Code of Practice on the Packaging, Handling and Storage of Chemical Wastes	Deficiency of mitigation measures but rectified by the Contractor
7.6.1	WM5	Sewage						
		An adequate number of portable toilets will be provided at the site to ensure that sewage from site staff is properly collected. The portable toilets will be desludged and maintained regularly by a specialist contractor.	To ensure proper handling of sewage	SENTX Site	SENTX Contractor	✓	WDO EIAO-TM Annex 7	Implemented
7.6.1 and	WM6	General Refuse						
SENTX latest design		General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to a transfer station or other landfill, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	handling of	SENTX Site	SENTX Contractor	~	WDO EIAO-TM Annex 7	Deficiency of mitigation measures but rectified by the Contractor
		Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the SENTX Site. Materials recovered will be sold for recycling.						
7.6.1	WM7	<u>Staff Training</u> At the commencement of the construction	To ensure that	SENTX Site	SENTX	$\checkmark$		Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main	Location of the Measures	Who to implement the measure?	the m	neas	implement ure? <sup>(1)</sup>	or standards for the	Implementation Status and Remarks
_			Concerns to address		the measure?	D	С	O/R A	measure to achieve?	
		works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	adverse environmental impacts are prevented		Contractor					
7.8	WM8	Environmental Monitoring & Audit Requirements Weekly audits of the waste management practices will be carried out during the construction phase. The audits examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	To ensure that adverse environmental impacts are prevented	SENTX Site	SENTX Contractor		✓		WDO	Implemented
Waste Ma	anagemen	t - Operation/Restoration Phase								
7.6.2 and SENTX latest design	WM9	Sludge In case off-site disposal is required, the Contractor will ensure that sludge generated from the LTP will be delivered in closed container to other waste disposal facility e.g. other landfills or a sludge treatment facility, for proper disposal on a daily basis.	To ensure proper handling of sludge	SENTX Site	SENTX Contractor			✓	WDO EIAO-TM Annex 7	Implemented
7.6.2	WM10	<u>Chemical Waste</u> The construction contractor will register as a chemical waste producer with the EPD. Chemical waste will be handled in	To ensure proper handling of chemical waste	SENTX Site	SENTX Contractor			V	WDO EIAO-TM Annex 7	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement	the m	ieasi	impleme ure? <sup>(1)</sup>		What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address		the measure?	D	С	O/R	4	measure to achieve?	
		accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes.								Code of Practice on the Packaging, Handling and Storage of Chemical Wastes	
7.6.2	WM11	<u>Sewage</u>									Moved to mitigation
		All sewage from the operation staff will be	To ensure proper	SENTX Site	SENTX			✓		WDO	measure under water quality WQ19. It is a
		diverted to the LTP for treatment or public sewer, if available.	handling of sewage		Contractor					EIAO-TM Annex 7	quality rrg12 h is a measure for water quality rather than waste management.
7.6.2 and	WM12	<u>General Refuse</u>									Implemented
SENTX latest		General refuse will be stored in enclosed bins		SENTX Site	SENTX			$\checkmark$		WDO	
design		and disposed of at other landfills or transfer station on a daily basis to reduce odour, pest and litter impacts.	handling of general refuse		Contractor					EIAO-TM Annex 7	
		Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the SENTX Site. Materials recovered will be sold for recycling.									
Landfill G	Gas Hazaı	rds - Design and Construction Phase									
8.6.2 and SENTX latest design	LFG1	Precautionary measures to be adopted by the contractors at the Project site and the adjacent development site within the landfill consultation zone are outlined in Paragraphs 8.3 to 8.49 of EPD's <i>Landfill Gas Hazard Assessment Guidance Notes</i> (the Guidance Note).		All construction works area	SENTX Contractor		✓			Paragraphs 8.3 to 8.49 of EPD's Landfill Gas Hazards Assessment Guidance Note EIAO-TM Annex 7	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the m	neas	<b>impler ure?</b> <sup>(1)</sup> O/R		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		Those precautionary measures applicable to the SENTX will be confirmed in the detailed Qualitative Landfill Gas Hazard Assessment to be submitted by the contractor.									
8.6.2	LFG2	Monitoring will be undertaken when construction works are carried out in confined space within the consultation zone with reference to the monitoring requirements and procedures specified in Paragraphs 8.23 to 8.28 of EPD's <i>Guidance</i> <i>Note</i> will be followed.	To protect workers from landfill gas risk	Confined space within the construction works area	SENTX Contractor		✓				Implemented
		In the event of the trigger levels being exceeded, it is recommended that a person, such as the Safety Officer, is nominated, with deputies, to be responsible for dealing with any emergency which may occur due to landfill gas. In an emergency situation, the nominated person, or his deputies, shall have the necessary authority and shall ensure that the confined space is evacuated and the necessary works implemented for reducing the concentrations of gas. The appropriate organisations shall be contact.									
8.6.3	LFG4	Implementation of engineering measures according to Contract Specification requirements. These measures will include the placement of liner and installation of landfill gas management system to contain, manage and control landfill gas.	To protect workers from landfill gas risk	SENTX Site	SENTX Contractor	~	✓	✓	•	EIAO-TM Annex 7	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement			imple sure? <sup>(1)</sup>		What requirements or standards for the	Implementation Status and Remarks
	Kei	Miligation Measures	Measure & Main Concerns to address	the measures	the measure?		C	O/R		measure to achieve?	
8.6.3	LFG5	Engineering measures to significant engineering measures will be required in the design of the SENTX to protect the staff working in the infrastructure area. These	To protect workers from landfill gas risk	Infrastructure Area	SENTX Contractor	•	✓			EPD's Landfill Gas Hazards Assessment Guidance Note EIAO-TM Annex 7	Implemented
		measures include a combination of passive and active systems (examples are recommended in EPD's <i>Guidance Notes</i> ).								EIAO-11vi Annex 7	
		Landfill gas monitoring boreholes will be installed at the edge of the waste slope between the waste and the new infrastructure area to monitor the migration of landfill gas, if any.									
Landfill ( Phases	Gas Hazai	rds – Operation, Restoration and Aftercare									
8.6.4	LFG7	To train and ensure staff to take appropriate precautions at all times when entering enclosed spaces or plant rooms. Undertake regular monitoring of landfill gas at the perimeter boreholes to detect if there are any signs of off-site landfill gas migration. Prepare and implement emergency plan in case off-site landfill gas migration is detected.	To protect workers from landfill gas risk	SENTX Site	SENTX Contractor			*	~	Landfill Gas Hazards Assessment Guidance Note	Implemented
8.7 and	LFG8	A permanent gas monitoring system with alarm will be installed and operated in all occupied on-site buildings. Environmental Monitoring & Audit	To protect	Within the	SENTX			✓	✓		Implemented
SENTX latest design		Requirements Undertake regular monitoring of landfill gas	workers from landfill gas risk	SENTX and along the SENTX	Contractor						•

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the 1		implen sure? <sup>(1)</sup> O/R	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		within the SENTX and along the SENTX boundary as required by the Contract Specification.		boundary					Landfill Gas Hazards Assessment Guidance Note	
Ecology -	Construc	tion Phase								
9.10.2	EC1	Measures to control construction runoff:	To minimise	All	SENTX		✓		EIAO-TM Annex 16	Implemented
		• Exposed soil areas will be minimised to	potential water quality impacts	construction works area	Contractor				ProPECC PN 1/94	
		reduce the contamination of runoff and erosion;	affecting ecological resources						Water Pollution Control Ordinance (WPCO)	
									EIAO-TM Annex 6	
		• To prevent stormwater runoff from washing across exposed soil surfaces, perimeter channels will be constructed in advance of site formation works and earthworks and intercepting channels will be provided for example along the edge of excavation;							-	Implemented
		• Silt removal facilities, channels and manholes will be maintained and the deposited silt and grit will be removed regularly to ensure they are functioning properly at all times;							-	Deficiency of mitigation measures but rectified by the Contractor
		• Temporary covers such as tarpaulin will also be provided to minimise the generation of high suspended solids							-	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the m	easure?	lement (1) 'R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		<ul> <li>runoff;</li> <li>The surface runoff contained any oil and grease will pass through the oil interceptors; and,</li> </ul>							-	Implemented
		• Control measures, including implementation of excavation schedules, lining and covering of excavated stockpiles will be implemented to minimise contaminated stormwater run-off from the SENTX site.							-	Implemented
9.10.2 and SENTX latest design	EC2	<ul> <li>Good Construction Practice:</li> <li>Fences along the boundary of the SENTX Site will be erected before the commencement of works to prevent vehicle movements, and encroachment of personnel, onto adjacent areas.</li> <li>The work site boundaries will be regularly checked to ensure that they are not breached and that damage does not occur to surrounding areas.</li> </ul>	To minimise potential ecological impacts arising from the Project	SENTX Site	SENTX Contractor		/		EIAO-TM Annex 16	Implemented
Ecology -	Operatio	n, Restoration and Aftercare Phases								
9.10.2	EC3	Measures for Controlling Leakage of Landfill Leachate Leachate will be contained within the SENTX Site by the proposed impermeable leachate containment system and collected by the	To minimise potential water quality impact affecting the	SENTX Site	SENTX Contractor		~	V	EIAO-TM Annex 16 WPCO Water-TM	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement	When to the mea	-		What requirements or standards for the	Implementation Status and Remarks
	Kei	Witigation Weasures	Measure & Main Concerns to address	the measures	the measure?		O/R		measure to achieve?	Status and Kentarks
		installation of drainage system to prevent potential migration of leachate to habitats in the vicinity.	ecological resources						EIAO-TM Annex 6	
9.10.2	EC4	<u>Measures for Controlling Migration of</u> Landfill Gas								Implemented
		Disturbance to habitat in the vicinity and associated wildlife due to migration of landfill gas will be prevented by proper management of the landfill gas generated from the SENTX. Ignition fires will be prohibited to occur within the boundary of the SENTX Site. Surface emission and off- site migration of landfill gas will be regularly monitored.	To minimise potential landfill gas migration affecting ecological resources	SENTX Site	SENTX Contractor		*	•	EIAO-TM Annex 16	
9.10.3 and SENTX latest design	EC5	<ul> <li>The following compensation planting is recommended as the mitigation measures for the habitat affected due to the SENTX:</li> <li>Provision of 6 ha of mixed woodland planting to compensate the loss of</li> </ul>	Compensation of habitat loss due to the Project	SENTX Site	SENTX Contractor		*	~	EIAO-TM Annex 16	Implemented
		shrubland; and								
9.10.3	EC6	<ul> <li>Provision of a mosaic of grassland and shrubland in the remaining areas of the SENTX Site.</li> <li>Compensatory planting and restoration of the SENTX can be implemented progressively according to the filling plan of SENTX.</li> <li>The mixture of grassland, shrubland and woodland habitats are recommended to diversify the habitats for supporting various wildlife in particular butterflies, birds and</li> </ul>	To diversify habitats	SENTX Site	SENTX Contractor		×	V	EIAO-TM Annex 16	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the m	ieasi	implen ure? <sup>(1)</sup> O/R		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		herpetofauna and blend into the existing undisturbed ecological environment.									
9.10.3	EC7	Indigenous plant species of shallow root system, softwood in nature and adaptive to sea shore habitat are recommended to be used in the restoration plan, which can establish well in coastal area with exposure to strong wind and salt spray, with sand soil base. Taking consideration of the relative poor substrate and the difficulties of establishment of some native trees in Hong Kong, it is recommended to include approximately 20% of non-native tree species in the compensatory woodland. The non- native tree species can serve as a nurse species to facilitate the establishment of the native tree species, especially the shading, and it can be replaced by established native tree species progressively. Plant species can also make reference to food plants of butterfly species (in particularly butterfly species of conservation interests recorded within the	To enhance ecological value of the habitats	SENTX Site	SENTX Contractor			<ul> <li>Image: A second s</li></ul>	•	EIAO-TM Annex 16	Implemented
9.10.3	EC8	CWBCP). It is also recommended that a trial nursery for native plant species be set up to fine tone the planting matrix and management intensity of the recommended indigenous tree species for the restoration of the SENTX. It should be noted that native shrubs and tree species had been used for restoration of the existing SENT Landfill, native plant species that could not	To select the most suitable indigenous tree species for the SENTX	SENTX Site	SENTX Contractor	✓		✓	•	EIAO-TM Annex 16	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the n		<b>impleı ure?</b> <sup>(1)</sup> O/R		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		successfully be established on the existing SENT Landfill should be reviewed before the preparation of the compensatory planting list. Special care and intensive management of native plant should be implemented in order to ensure proper establishment of the native plants.									
9.12.1	EC9	Environmental Monitoring & Audit Requirements The implementation of the ecological mitigation measures should be checked as part of the environmental monitoring and audit procedures during the construction period.	To ensure that adverse ecological impacts are prevented	SENTX	SENTX Contractor		✓	✓	~	EIAO-TM Annex 16	Implemented
Landscap	e and Vis	ual – Construction Phase									
10.6.5	LV1	CM1 - The construction area and area allowed for the contractor's office, leachate treatment plant and laboratory areas will be minimised to a practical minimum, to avoid impacts on adjacent landscape.	To minimise the landscape and visual impacts	SENTX Site	SENTX Contractor		✓			EIAO-TM Annex 18 and ETWBC 3/2006	Implemented
10.6.5	LV2	CM2 - Topsoil, where identified, will be stripped and stored for re-use in the construction of the soft landscape works, where practical. The Contract Specification will include storage and reuse of topsoil as appropriate.	To minimise the landscape and visual impacts	All construction works area	SENTX Contractor		✓			EIAO-TM Annex 18	Not applicable
10.6.5	LV3	CM3 - All existing trees at the edges of the landfill will be carefully protected during	To minimise the landscape and	Potential impacted area	SENTX Contractor		✓			EIAO-TM Annex 18 and ETWBC 3/2006	Not applicable

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement	the	meas	implement sure? <sup>(1)</sup>	or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address		the measure?	D	C	O/R A	measure to achieve?	
		construction. Detailed Tree Protection Specification will be provided in the Contract Specification. Under this Specification, the Contractor will be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in Contractor's works areas.	visual impacts							
10.6.5	LV4	CM4 - Trees unavoidably affected by the works will be transplanted, where necessary and practical. A detailed Tree Transplanting Specification will be provided in the Contract Specification, if applicable. Sufficient time for necessary tree root and crown preparation periods will be allowed in the project programme.	To minimise the landscape and visual impacts	Potential impacted area	SENTX Contractor	~	~		EIAO-TM Annex 18 and ETWBC 3/2006	Implemented
10.6.5 and SENTX latest design	LV5	CM5 - Within 3 months of taking possession of the SENTX Site, the Contractor will plant advance screen planting of native species at Light Standard size at 1.5m centres along the High Junk Peak Trail so as to screen views of the Works from the trail. Tree planting locations will be agreed with AFCD. Works will be completed within 9 months of taking possession of the SENTX Site.	To minimise the landscape and visual impacts	At High Junk Peak Hiking Trail	SENTX Contractor		~		EIAO-TM Annex 18	Implemented
10.6.5	LV6	CM6 - The Contractor's office, leachate treatment plant and laboratory will be given an aesthetic treatment in earth tones to reduce their visual impact and albedo and blend	To minimise the landscape and visual impacts	Infrastructure area	SENTX Contractor	✓	~		EIAO-TM Annex 18	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the		o implement sure? <sup>(1)</sup> O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		them into the surrounding landscape.								
10.6.5	LV7	CM7 - The Contractor's office, leachate treatment plant and laboratory will be surrounded by a minimum of 5m wide and 0.75m high earth bund on the west and south sides planted with a dense screen of tree and shrub vegetation. Additional tree planting will be provided in unused spaces with thin infrastructure site, along access roads and in and around car parks. This will be supplemented with shrub planting, where appropriate.	To minimise the landscape and visual impacts	Infrastructure area	SENTX Contractor	•	~		EIAO-TM Annex 18 and ETWBC 7/2002	Not applicable
10.6.5	LV8	CM8 - Planting trials will be carried out in an on-site nursery prior to implementation of the first phase of restoration to establish the best planting matrix and management intensity of the recommended plant materials for the restoration.	landscape and	SENTX Site	SENTX Contractor		~		EIAO-TM Annex 18	Implemented
11.4.1 and SENTX latest design	LV9	During the preparation of the detailed landscape design plan, the design submission will be audited against the recommendation proposed in the <i>ER Report</i> by the Registered Landscape Architect from the ET.	To ensure the implementation of mitigation measures proposed in this EIA Report	SENTX Site	SENTX Contractor/E T	•	•		EIAO-TM Annex 18	Implemented
Landscap	e and Visi	ual - Operation/Restoration Phase								
10.6.5 and SENTX	LV10	OM1 - Landfill materials will be covered with general fill material or tarpaulin sheet on a daily basis to reduce visual impact.	To minimise the landscape and visual impacts	Tipping area	SENTX Contractor			V	EIAO-TM Annex 18	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to the mea D C	o implement sure? <sup>(1)</sup> O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
latest design									
10.6.5 and SENTX latest design	LV11	OM2 - Filling and restoration will be phased during the course of operations in a minimum of 4 phases, the restoration of each phase to commence immediately on the completion of filling in that phase.	To minimise the landscape and visual impacts	Tipping area	SENTX Contractor		~	EIAO-TM Annex 18	Implemented
10.6.5	LV12	OM3 - Catch fences will be erected at the perimeter of the waste boundary, to ensure that all waste stays within the site and is not blown into surrounding areas.	To minimise the landscape and visual impacts	Tipping area	SENTX Contractor		✓	EIAO-TM Annex 18	Implemented
10.6.5	LV13	OM4 - All night-time lighting will be reduced to a practical minimum both in terms of number of units and lux level and will be hooded and directional.	To minimise the landscape and visual impacts	Tipping area	SENTX Contractor		✓	EIAO-TM Annex 18	Implemented
11.4.2 and SENTX latest design	LV14	The condition of the restoration plantation will be audited at monthly intervals by a Registered Landscape Architect from the ET.	To check the restoration plantation	SENTX Site	SENTX Contractor/E T		✓	EIAO-TM Annex 18	Implemented

Annex C

Monitoring Schedule for This Reporting Period

#### South East New Territories (SENT) Landfill Extension EM&A Impact Monitoring Schedule during Construction Phase

Sun	Mon	Tue	Wed	Thu	Fri	Sat
					1	2
2	4	5		7	8	9
Dust Monitoring	4	5	6	Surface Water Monitoring (pm)	0	9
				Noise Monitoring (pm)		
10	11	12	13	14	15	16
	Dust Monitoring				Surface Water Monitoring (pm)	
					Noise Monitoring (pm)	
					Dust Monitoring	
17	18	19	20		22	23
				Surface Water Monitoring (pm)		
				Noise Monitoring (pm) Dust Monitoring		
24	25	26	27		29	30
24	25	20	Dust Monitoring	Surface Water Monitoring (pm)	29	50
				Noise Monitoring (pm)		
31						

October 2021

Note:

Impact dust monitoring will be conducted at two monitoring stations (DM1 and DM2) under the on-going EM&A programme TKO Area 137 Fill Bank and the results will be shared with SENTX.

#### South East New Territories (SENT) Landfill Extension

EM&A Impact Monitoring Schedule during Construction Phase (1 - 20 Nov 2021) & Operation/ Restoration Phase (21 - 30 Nov 2021)

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2	3	4	5	6
		Dust Monitoring *		Surface Water Monitoring		
				Noise Monitoring		
7	8	9	10	11	12	13
	Dust Monitoring *			Surface Water Monitoring		
				Noise Monitoring		
14	15	16	17	18	19	20
Dust Monitoring *				Surface Water Monitoring		Dust Monitoring *
				Noise Monitoring		
21	22	23	24	25	26	27
Odour Monitoring	Odour Monitoring	Odour Monitoring				
Leachate Monitoring	Leachate Monitoring	Leachate Monitoring				
				Dust Monitoring		
				Surface Water Monitoring		
				Noise Monitoring		
28	29	30				
Odour Monitoring	Odour Monitoring	Odour Monitoring				
Leachate Monitoring	Leachate Monitoring	Leachate Monitoring				

November 2021

Note:

\*Impact dust monitoring will be conducted at two monitoring stations (DM1 and DM2) under the on-going EM&A programme TKO Area 137 Fill Bank and the results will be shared with SENTX.

#### South East New Territories (SENT) Landfill Extension EM&A Impact Monitoring Schedule during Operation/ Restoration Phase

Sun	Mon	Tue	Wed		Thu	Fri	Sat
				1	2		3 4
			Odour Monitoring		Odour Monitoring	Odour Monitoring	Odour Monitoring
			Leachate Monitoring		Leachate Monitoring	Leachate Monitoring	Leachate Monitoring
			Dust Monitoring		Noise Monitoring		
5	6	7		8	9	1	0 11
Odour Monitoring	Odour Monitoring	Odour Monitoring	Odour Monitoring		Odour Monitoring	Odour Monitoring	Odour Monitoring
Leachate Monitoring	Leachate Monitoring	Leachate Monitoring	Leachate Monitoring		Leachate Monitoring	Leachate Monitoring	Leachate Monitoring
		Dust Monitoring	Groundwater Monitoring		Noise Monitoring		
		Groundwater Monitoring					
12	13	14		15	16	1	7 18
Odour Monitoring	Odour Monitoring	Odour Monitoring	Odour Monitoring		Odour Monitoring	Odour Monitoring	Odour Monitoring
Leachate Monitoring	Leachate Monitoring	Leachate Monitoring	Leachate Monitoring		Leachate Monitoring	Leachate Monitoring	Leachate Monitoring
	Dust Monitoring	Noise Monitoring			Service Void LFG Monitoring	Stack Monitoring	
		Perimeter LFG Monitoring					
19	20	21		22	23	2	4 25
Odour Monitoring	Odour Monitoring	Odour Monitoring	Odour Monitoring		Odour Monitoring	Odour Monitoring	Odour Monitoring
Leachate Monitoring	Leachate Monitoring	Leachate Monitoring	Leachate Monitoring		Leachate Monitoring	Leachate Monitoring	Leachate Monitoring
Dust Monitoring	Stack Monitoring		Noise Monitoring				Dust Monitoring
	-						
26	27	28		29	30	3	1
Odour Monitoring	Odour Monitoring	Odour Monitoring	Odour Monitoring		Odour Monitoring	Odour Monitoring	
Leachate Monitoring	Leachate Monitoring	Leachate Monitoring	Leachate Monitoring		Leachate Monitoring	Leachate Monitoring	
		Noise Monitoring				Dust Monitoring	
		Surface Water Monitoring					

December 2021


### Air Quality

### 24-hour TSP Monitoring Results

Start Date	Start Time	Finish Date	Finish Time	Weather	24-hour TSP (μg/m3)
3 Oct 21	13:00	4 Oct 21	13:00	Rainy	92
11 Oct 21	10:20	12 Oct 21	10:20	Fine	112
15 Oct 21	16:00	16 Oct 21	16:00	Fine	95
21 Oct 21	8:00	22 Oct 21	8:00	Rainy	92
27 Oct 21	13:33	28 Oct 21	13:33	Fine	99
2 Nov 21	13:00	3 Nov 21	13:00	Fine	109
8 Nov 21	8:30	9 Nov 21	8:30	Fine	94
14 Nov 21	13:00	15 Nov 21	13:00	Fine	102
20 Nov 21	8:00	21 Nov 21	8:00	Fine	99
				Average	99
				Min	92
				Max	112
Note:					
DM1 corres	ponds to the	existing TSP r	nonitoring stat	ion TKO-A1 c	urrently operating by
CEDD.			-		

#### Table D1.1 24-hour TSP Monitoring Results at DM1 (During Construction Phase)

*Figure D1.1 Graphical Presentation for 24-hr TSP Monitoring at DM1 (During Construction Phase)* 

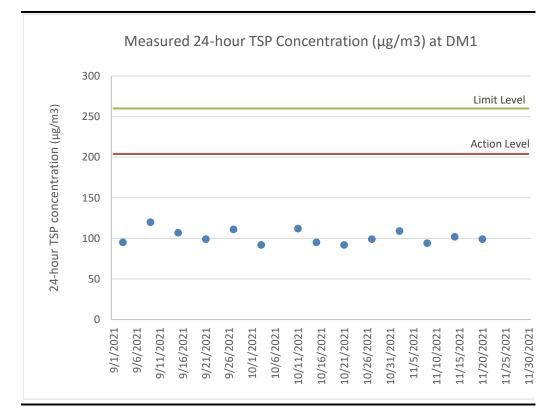


#### Table D1.2 24-hour TSP Monitoring Results at DM2 (During Construction Phase)

Start Date	Start Time	<b>Finish Date</b>	Finish Time	Weather	24-hour TSP (µg/m3)
3 Oct 21	13:00	4 Oct 21	13:00	Rainy	87
11 Oct 21	10:30	12 Oct 21	10:30	Fine	104
15 Oct 21	16:00	16 Oct 21	16:00	Fine	90
21 Oct 21	8:00	22 Oct 21	8:00	Rainy	86
27 Oct 21	13:44	28 Oct 21	13:44	Fine	93
2 Nov 21	13:00	3 Nov 21	13:00	Fine	97
8 Nov 21	8:35	9 Nov 21	8:35	Fine	86
14 Nov 21	13:00	15 Nov 21	13:00	Fine	90
20 Nov 21	8:00	21 Nov 21	8:00	Fine	89
				Average	91
				Min	86
				Max	104


DM2 corresponds to the existing TSP monitoring station TKO-A2a currently operating by CEDD.

# *Figure D1.2 Graphical Presentation for 24-hr TSP Monitoring at DM2 (During Construction Phase)*

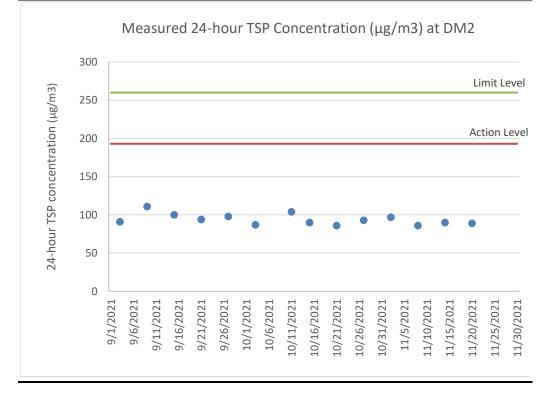

Start Date	Start Time	Finish Date	Finish Time	Weather	24-hour TSP (µg/m3)
25 Nov 21	9:00	26 Nov 21	9:00	Sunny	100
1 Dec 21	9:00	2 Dec 21	9:00	Sunny	57
7 Dec 21	9:00	8 Dec 21	9:00	Sunny	141
13 Dec 21	9:00	14 Dec 21	9:00	Sunny	173
19 Dec 21	9:00	20 Dec 21	9:00	Sunny	114
25 Dec 21	9:00	26 Dec 21	9:00	Fine	64
31 Dec 21	9:00	1 Jan 22	9:00	Fine	125
				Average	111
				Min	57
				Max	173

*Figure D1.3 Graphical Presentation for 24-hr TSP Monitoring at AM1 (During Operation Phase)* 

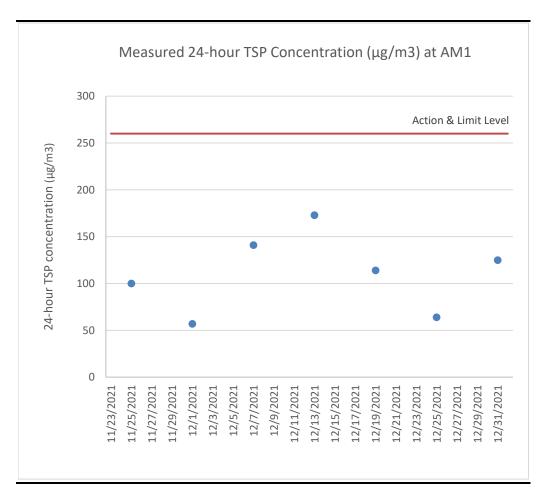

#### Table D1.4 24-hour TSP Monitoring Results at AM2 (During Operation Phase)

Start Date	Start Time	Finish Date	Finish Time	Weather	24-hour TSP (µg/m3)
25 Nov 21	9:00	26 Nov 21	9:00	Sunny	154
2 Dec 21*	15:00	3 Dec 21	15:00	Sunny	115
7 Dec 21	9:00	8 Dec 21	9:00	Sunny	156
13 Dec 21	9:00	14 Dec 21	9:00	Sunny	152
19 Dec 21	9:00	20 Dec 21	9:00	Sunny	133
25 Dec 21	9:00	26 Dec 21	9:00	Fine	120
31 Dec 21	9:00	1 Jan 22	9:00	Fine	100
				Average	133
				Min	100
				Max	156
Notes:					

\* Sampling was suspended due to equipment failure.

# *Figure D1.4 Graphical Presentation for 24-hr TSP Monitoring at AM2 (During Operation Phase)*


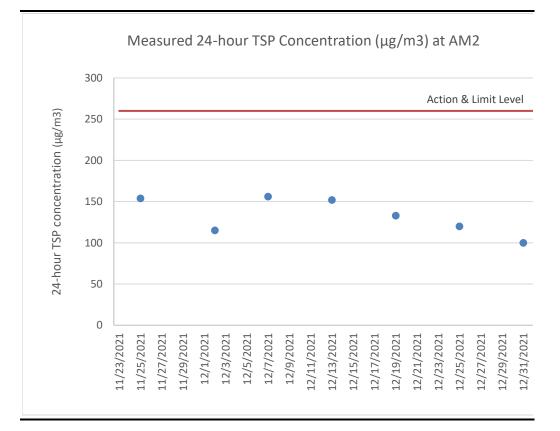


Table D1.524-hour TSP Monitoring	Results at AM3 (During Operation Phase)
----------------------------------	---

Start Date	Start Time	<b>Finish Date</b>	Finish Time	Weather	24-hour TSP (µg/m3)
25 Nov 21	16:30	26 Nov 21	16:30	Sunny	158
1 Dec 21	9:00	2 Dec 21	9:00	Sunny	128
7 Dec 21	9:00	8 Dec 21	9:00	Sunny	169
13 Dec 21	8:05	14 Dec 21	8:05	Sunny	258
19 Dec 21	9:00	20 Dec 21	9:00	Sunny	191
25 Dec 21	9:00	26 Dec 21	9:00	Fine	189
31 Dec 21	14:25	1 Jan 22	14:25	Fine	155
				Average	178
				Min	128
				Max	258


*Figure D1.5 Graphical Presentation for 24-hr TSP Monitoring at AM3 (During Operation Phase)* 

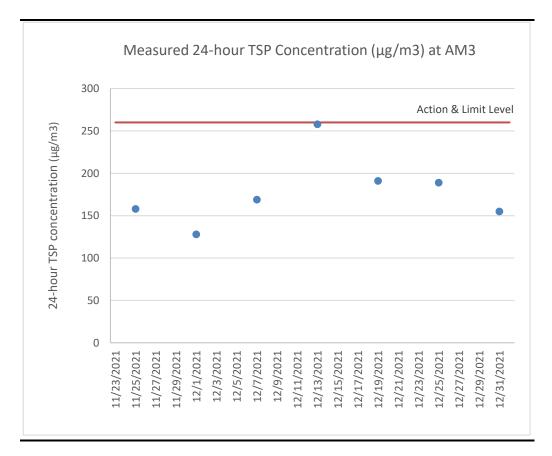

#### Table D1.624-hour TSP Monitoring Results at AM4 (During Operation Phase)

Start Date	Start Time	<b>Finish Date</b>	Finish Time	Weather	24-hour TSP (µg/m3)
25 Nov 21	9:00	26 Nov 21	9:00	Sunny	235
1 Dec 21	9:00	2 Dec 21	9:00	Sunny	206
7 Dec 21	9:00	8 Dec 21	9:00	Sunny	164
13 Dec 21	9:00	14 Dec 21	9:00	Sunny	282
19 Dec 21	9:00	20 Dec 21	9:00	Sunny	129
25 Dec 21	9:00	26 Dec 21	9:00	Fine	102
31 Dec 21	9:00	1 Jan 22	9:00	Fine	125
				Average	178
				Min	102
				Max	282

*Figure D1.6 Graphical Presentation for 24-hr TSP Monitoring at AM4 (During Operation Phase)* 

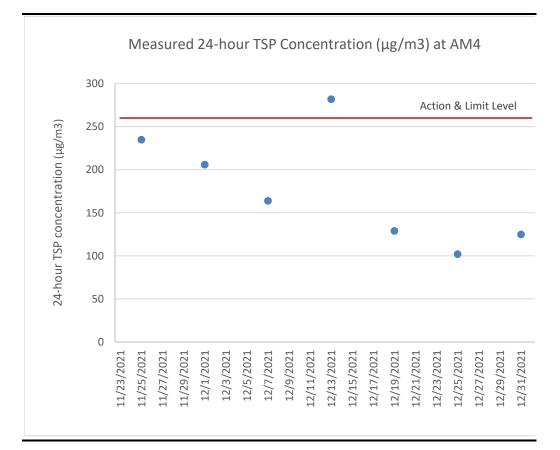

## Event and Action Plan for Air Quality Monitoring

Action					
Event	ET	IEC	Contractor		
Action Level					
Exceedance for one sample	<ul> <li>Identify the source(s) and investigate the cause(s) of exceedance</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project</li> <li>Repeat measurement to confirm finding if exceedance is due to the Project</li> <li>Increase monitoring frequency to daily if exceedance is due to the Project and continue until the monitoring results reduce to below action level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working methods</li> </ul>	<ul><li>Rectify any unacceptable practice</li><li>Amend working methods if appropriate</li></ul>		
Exceedance for two or more consecutive samples	<ul> <li>Identify the source(s) and investigate the cause(s) of exceedance</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>If exceedance continues, arrange meeting with Contractor &amp; IEC</li> <li>Continue monitoring at daily intervals if exceedance is due to the Project</li> <li>If no exceedance for 3 consecutive days, cease additional monitoring</li> </ul>	Check monitoring data submitted by ET	<ul> <li>Submit proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate</li> </ul>		

### Annex D2a Event and Action Plan for Dust Monitoring During Construction Phase

		Action	
Event	ET	IEC	Contractor
Limit Level			
Exceedance for one sample	<ul> <li>Identify the source(s) and investigate the cause(s) of exceedance</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Repeat measurement to confirm finding if exceedance is due to the Project</li> <li>Increase monitoring frequency to daily if exceedance is due to the Project and continue until the monitoring results reduce to below limit level</li> </ul>	<ul><li>Check monitoring data submitted by ET</li><li>Check Contractor's working methods</li></ul>	<ul> <li>Take immediate action to avoid further exceedance</li> <li>Submit proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate</li> </ul>
Exceedance for two or more consecutive samples	<ul> <li>Identify source(s) and investigate the cause(s) of exceedance</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD the causes &amp; actions taken for the exceedances</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Continue monitoring at daily intervals if exceedance is due to the Project</li> <li>If no exceedance for 3 consecutive days, cease additional monitoring</li> <li>If exceedance due to the Project continues, consider what portion of the work is responsible and stop that portion of work until the exceedance is abated</li> </ul>		<ul> <li>Take immediate action to avoid further exceedance</li> <li>Submit proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> <li>Resubmit proposals if problem still not under control</li> </ul>

		Action	
Event	ET	IEC	Contractor
Exceedance of Action/Limit Level for dust monitoring	<ul> <li>Identify the source(s) and investigate the cause(s) of exceedance</li> <li>Prepare the Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures</li> <li>Ensure remedial measures are properly implemented</li> <li>Assess effectiveness of Contractor's remedial measures and keep the Project Proponent and IEC informed of the results</li> <li>Repeat measurement to confirm finding if exceedance is due to the Project</li> <li>Increase monitoring frequency to daily and continue until the monitoring results reduce to below action level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working methods</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Take immediate action to avoid further exceedance</li> <li>Submit proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate</li> </ul>
Exceedance of Action Level for odour	<ul> <li>Identify source(s) and investigate the cause(s) of exceedance or complaint</li> <li>Prepare the odour complaint form or the Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures</li> <li>Ensure remedial measures are properly implemented</li> <li>Increase monitoring frequency to daily until odour not being detected for three consecutive days</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working methods</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Rectify any unacceptable practice</li> <li>Amend working methods as required</li> <li>Implement amended working methods, if necessary</li> </ul>

### Annex D2b Event and Action Plan for Air Quality Monitoring During Operation/Restoration Phase


		Action	
Event	ET	IEC	Contractor
Exceedance of Limit Level for odour	<ul> <li>Identify source(s) and investigate the cause(s) of exceedance or complaint</li> <li>Prepare the odour complaint form or the Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures</li> <li>Ensure remedial measures are properly implemented</li> <li>Assess effectiveness of Contractor's remedial measures and keep the Project Proponent and IEC informed of the results</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check with Contractor on the operating activities and implementation of odour mitigation measures</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Rectify any unacceptable practice</li> <li>Submit proposals for remedial measures to IEC within 3 working days of notification</li> <li>Implement the agreed proposal or amend working methods as required</li> <li>Resubmit proposals if problem still not under control</li> </ul>
Exceedance of Limit Level for ambient VOCs, ammonia and H <sub>2</sub> S at the monitoring locations	<ul> <li>Identify the source(s) and investigate the cause(s) of exceedance</li> <li>Prepare the Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures</li> <li>Ensure remedial measures are properly implemented</li> <li>Assess effectiveness of Contractor's remedial measures and keep the Project Proponent and IEC informed of the results</li> <li>Repeat measurement to confirm finding if exceedance is due to the Project</li> <li>Increase monitoring frequency to monthly and continue until the monitoring results reduce to below limit level</li> </ul>	<ul> <li>Check with Contractor on the operating activities and implementation of landfill gas control measures</li> </ul>	<ul> <li>Rectify any unacceptable practice</li> <li>Amend working methods as required</li> <li>Implement amended working methods, if necessary</li> </ul>


Action				
Event	ET	IEC	Contractor	
Exceedance of Limit Level of stack emission of the thermal oxidizer, flares and generator	<ul> <li>Identify source(s) and investigate the cause(s) of exceedance</li> <li>Prepare the Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures</li> <li>Ensure remedial measures are properly implemented</li> <li>Assess effectiveness of Contractor's remedial measures and keep the Project Proponent and IEC informed of the results</li> <li>Repeat measurement to confirm finding if exceedance is due to the Project</li> <li>Increase monitoring frequency to monthly when there are two consecutive exceedances and continue until the monitoring results reduce to below limit level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check with Contractor on the operating performance of the stack</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Rectify any unacceptable performance</li> <li>Amend design as required</li> <li>Implement amended design, if necessar</li> </ul>	


## Meteorological Data


## Annex D3 Meteorological Data


<u>Oct 2021</u>

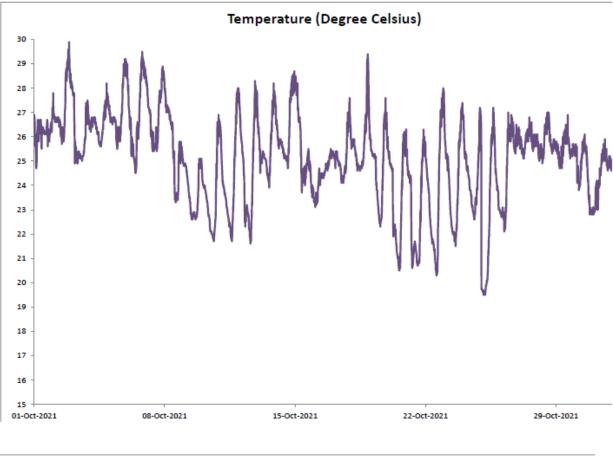


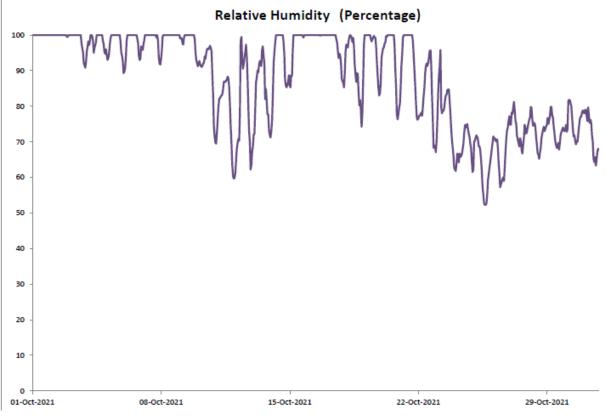


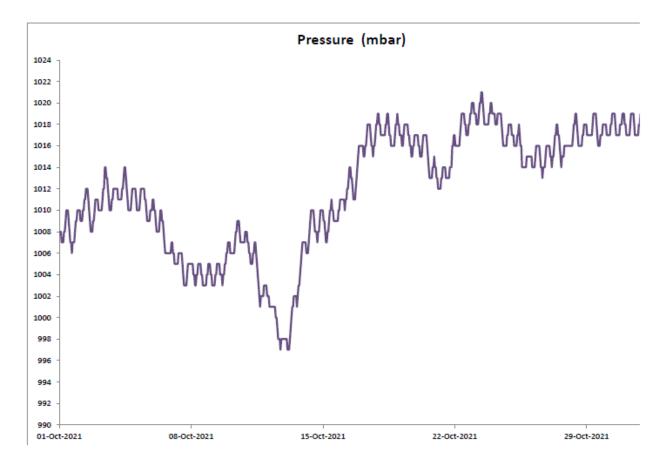

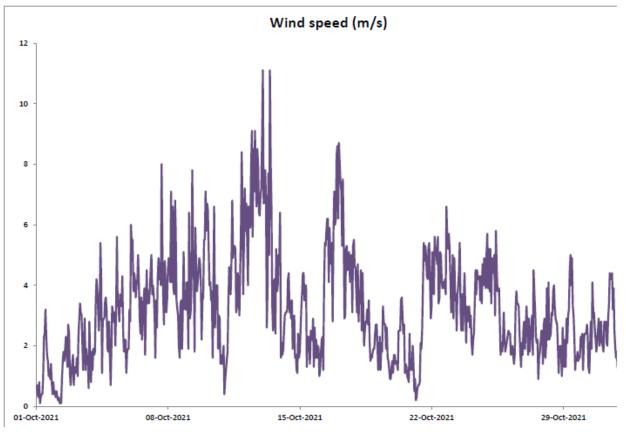


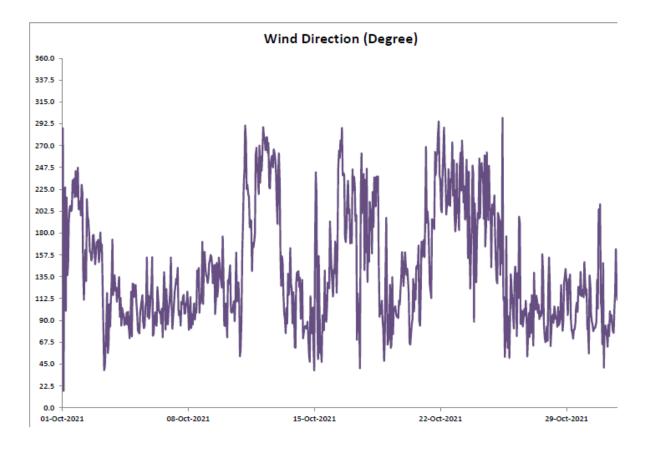


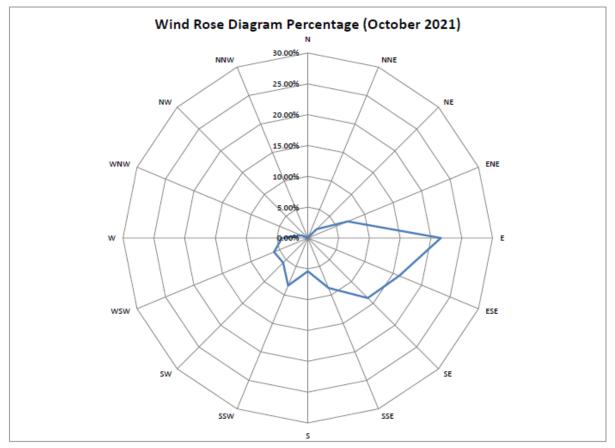


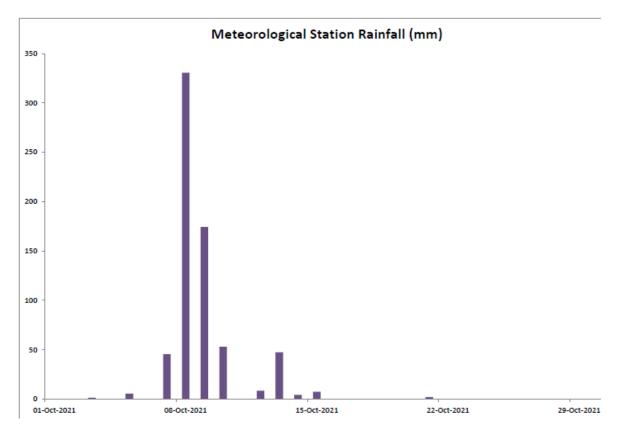



<u>Nov 2021</u>

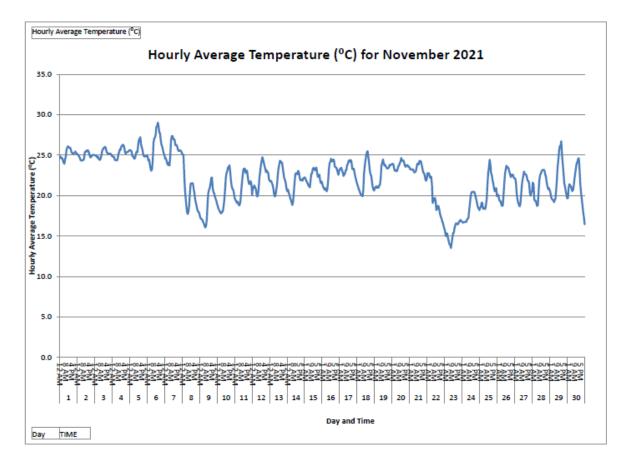


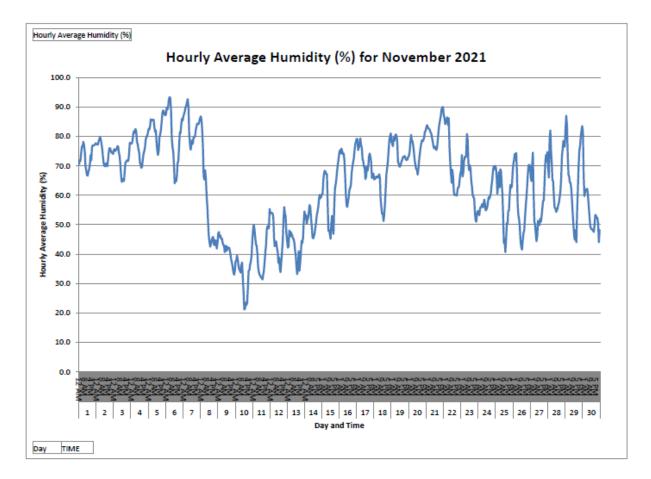


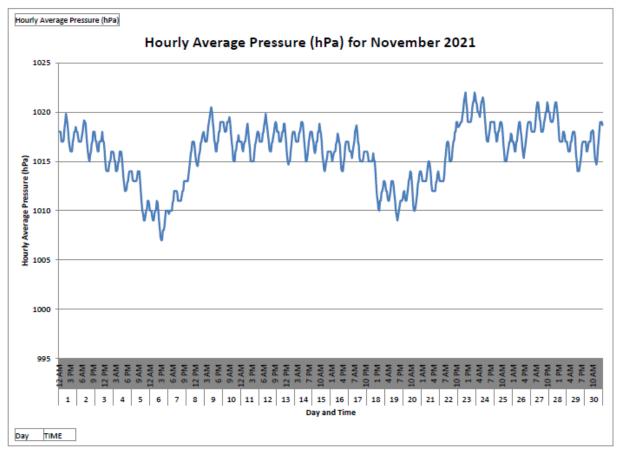


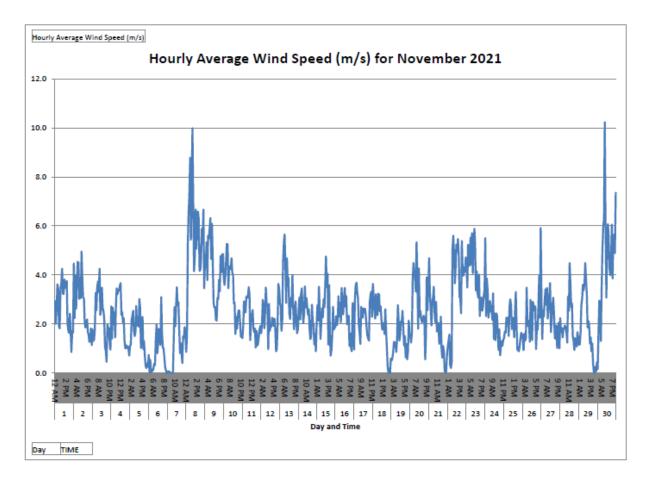


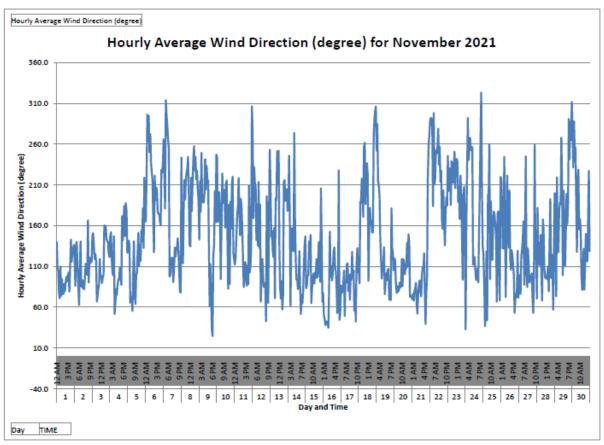


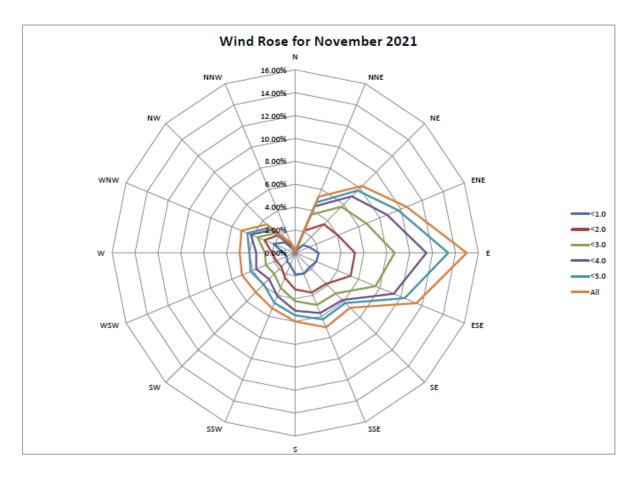


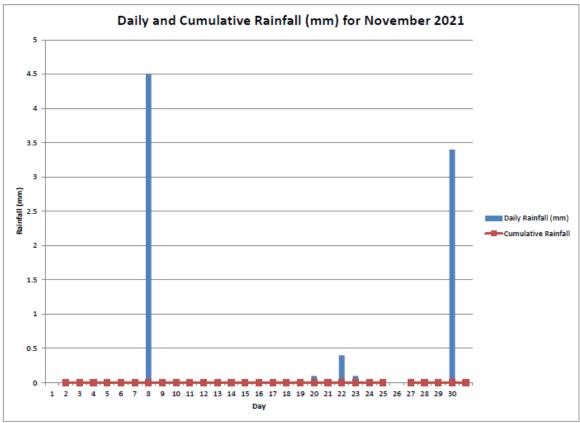


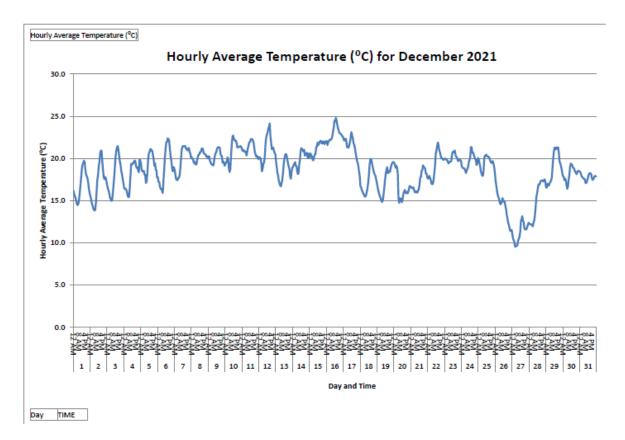


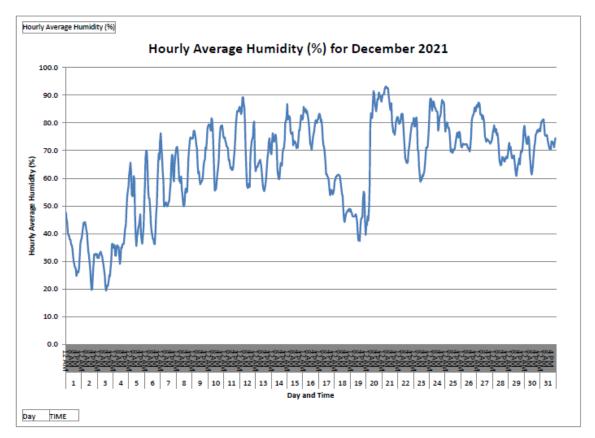


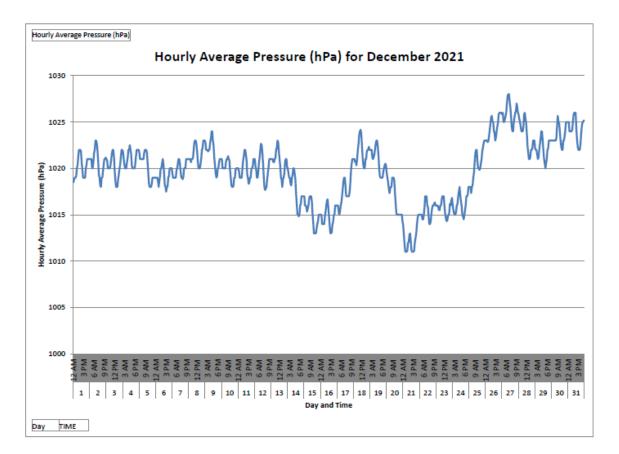

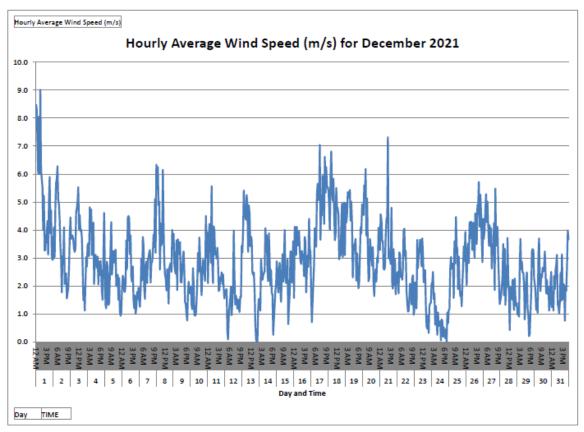

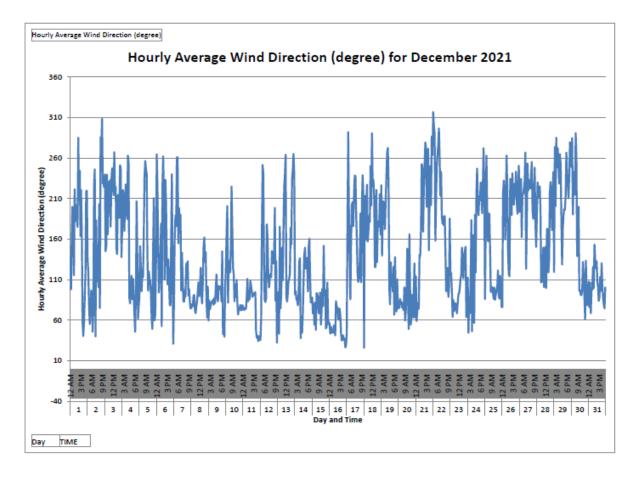

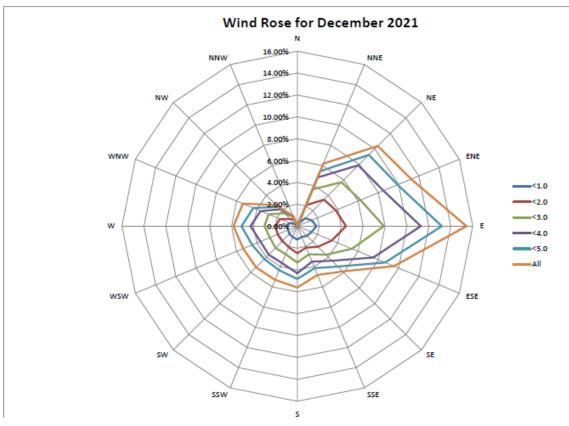

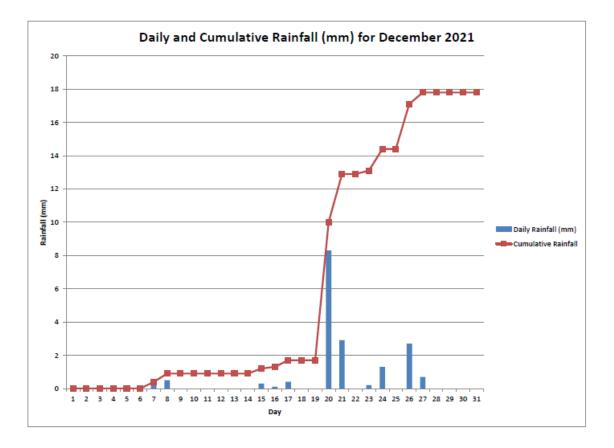

Annex D4

Odour Monitoring Results

# Table D4.1 Odour Monitoring Results

Date	Weather	Location	Time	Temperature	Wind Speed		From	Odour	Odour	Possible Source	Remarks
				(oC)	(m/s)	Direction	Project Site	5	Characteristic		
21 Nov 21	Sunny	OP1	10:06	27.6	2.4	Ν	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP2	10:15	28.8	1.0	Ν	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP3	10:20	28.3	1.3	NW	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP4	10:24	26.6	2.9	NE	No	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP5	10:28	26.1	3.5	NE	No	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP6	10:32	28.4	1.1	NW	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP7	10:39	29.8	1.3	Ν	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP8	10:42	29.3	1.3	S	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP9	10:48	30.8	1.5	NE	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP10	10:51	29.7	1.6	NE	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP1	14:03	29.5	1.3	Ν	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP2	14:06	29.7	0.9	Ν	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP3	14:10	28.2	1.4	S	No	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP4	14:14	28.7	2.1	Е	No	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP5	14:18	27.9	3.3	NE	Yes	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP6	14:22	28.2	3.3	S	No	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP7	14:25	29.2	2.9	S	No	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP8	14:30	28.1	2.4	Ν	No	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP9	14:35	27.7	3.3	Ν	No	0	N/A	N/A	N/A
21 Nov 21	Sunny	OP10	14:39	28.2	2.4	Е	Yes	0	N/A	N/A	N/A
21 Nov 21	Fine	OP1	18:05	24.0	0.1	NW	Yes	0	N/A	N/A	N/A
21 Nov 21	Fine	OP2	18:08	24.0	0.2	NW	Yes	0	N/A	N/A	N/A
21 Nov 21	Fine	OP3	18:12	23.4	0.4	NE	No	0	N/A	N/A	N/A
21 Nov 21	Fine	OP4	18:15	23.4	0.4	NE	No	0	N/A	N/A	N/A
21 Nov 21	Fine	OP5	18:18	23.7	0.8	NE	No	0	N/A	N/A	N/A
21 Nov 21	Fine	OP6	18:22	24.0	0.7	Ν	No	0	N/A	N/A	N/A
21 Nov 21	Fine	OP7	18:25	23.6	0.4	NW	No	0	N/A	N/A	N/A
21 Nov 21	Fine	OP8	18:29	23.5	0.9	Ν	No	0	N/A	N/A	N/A
21 Nov 21	Fine	OP9	18:34	23.6	0.7	SE	Yes	1	Gas (Pungent)	Town Gas Plant	N/A
21 Nov 21	Fine	OP10	18:38	23.5	0.5	SE	Yes	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP1	10:35	21.5	3.5	Ν	Yes	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP2	10:40	21.2	2.6	Ν	Yes	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP3	10:43	21.2	2.2	NE	No	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP4	10:46	21.8	1.3	Е	No	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP5	10:51	20.9	4.0	Ν	Yes	0	N/A	Ń/A	N/A

ENVIRONMENTAL RESOURCES MANAGEMENT

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
22 Nov 21	Overcast	OP6	10:55	20.4	5.2	Ν	No	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP7	10:58	20.4	2.3	Ν	No	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP8	11:03	20.5	3.6	Ν	No	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP9	11:08	20.9	2.5	Ν	No	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP10	11:14	22.2	0.5	Е	Yes	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP1	14:47	19.2	2.4	Ν	Yes	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP2	14:53	19.5	1.6	Ν	Yes	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP3	14:56	20.1	1	Ν	Yes	1	Exhaust gas	Generator	N/A
22 Nov 21	Overcast	OP4	15:00	20.5	1.8	NE	Yes	1	Biogas	Slurry Truck	N/A
22 Nov 21	Overcast	OP5	15:07	20.3	1.5	NE	Yes	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP6	15:10	19.4	2.5	Ν	No	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP7	15:14	19.3	3.3	Ν	No	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP8	15:18	19.5	2.4	NE	No	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP9	15:22	20.0	1.1	NE	No	0	N/A	N/A	N/A
22 Nov 21	Overcast	OP10	15:26	20.7	0.6	NE	No	0	N/A	N/A	N/A
22 Nov 21	Fine	OP1	18:07	21	3.3	Ν	Yes	0	N/A	N/A	N/A
22 Nov 21	Fine	OP2	18:10	21.3	2.5	Ν	Yes	0	N/A	N/A	N/A
22 Nov 21	Fine	OP3	18:14	22.3	2.4	Ν	Yes	1	Diesel	Generator	N/A
22 Nov 21	Fine	OP4	18:20	22	0.9	Ν	Yes	1	Biogas	Leachate Treatment Plant	
22 Nov 21	Fine	OP5	18:23	21.6	2.3	Ν	Yes	0	N/A	N/A	N/A
22 Nov 21	Fine	OP6	18:27	21.5	2.1	NW	No	0	N/A	N/A	N/A
22 Nov 21	Fine	OP7	18:30	20.9	1.7	NW	No	0	N/A	N/A	N/A
22 Nov 21	Fine	OP8	18:33	19.8	3.5	Ν	No	0	N/A	N/A	N/A
22 Nov 21	Fine	OP9	18:37	19.7	3.5	Ν	No	0	N/A	N/A	N/A
22 Nov 21	Fine	OP10	18:40	19.5	2.5	Ν	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP1	10:33	17.2	3.5	Ν	Yes	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP2	10:37	17.8	0.8	Ν	Yes	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP3	10:39	17.3	1.4	NE	No	1	Diesel	Generator	N/A
23 Nov 21	Overcast	OP4	10:42	17.2	1.1	Е	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP5	10:46	16.5	3.4	Ν	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP6	10:50	16.3	2.9	Ν	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP7	10:53	15.9	2	NE	Yes	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP8	10:57	15.7	2.5	Ν	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP9	11:01	16	2.5	Ν	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP10	11:05	16.4	1.8	Ν	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP1	14:40	18.3	3.8	Ν	Yes	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP2	14:44	18	2.2	Ν	Yes	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP3	14:47	17.9	2.4	NE	No	1	Diesel	Generator	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
23 Nov 21	Overcast	OP4	14:51	19.4	0.5	E	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP5	14:55	18.4	2.3	E	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP6	14:58	17.6	1.9	N	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP7	15:04	17.8	2.7	N	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP8	15:08	17.5	2.3	N	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP9	15:12	17.6	2.4	N	No	0	N/A	N/A	N/A
23 Nov 21	Overcast	OP10	15:15	18	0.6	N	No	0	N/A	N/A	N/A
23 Nov 21	Fine	OP1	18:10	20.5	2.2	NW	Yes	0	N/A	N/A	N/A
23 Nov 21	Fine	OP2	18:14	20.5	2.1	NW	Yes	0	N/A	N/A	N/A
23 Nov 21	Fine	OP3	18:18	21	1.7	NW	Yes	1	Diesel	Generator	N/A
23 Nov 21	Fine	OP4	18:23	21.8	0.8	NE	Yes	0	N/A	N/A	N/A
23 Nov 21	Fine	OP5	18:27	21.2	1.4	SE	No	0	N/A	N/A	N/A
23 Nov 21	Fine	OP6	18:31	20	2.4	N	No	0	N/A	N/A	N/A
23 Nov 21	Fine	OP7	18:35	18.5	1.9	N	No	0	N/A	N/A	N/A
23 Nov 21	Fine	OP8	18:39	19.4	1.9	N	No	0	N/A	N/A	N/A
23 Nov 21	Fine	OP9	18:44	18.4	1.5	N	No	0	N/A	N/A	N/A
23 Nov 21	Fine	OP10	18:48	18.9	2.1	N	No	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP1	10:32	21.9	1.3	N	Yes	1	Grass	Ground	N/A
24 Nov 21	Sunny	OP2	10:37	22.5	1.4	NW	Yes	1	Grass	Ground	Ň/A
24 Nov 21	Sunny	OP3	10:40	21.8	1.2	Ν	Yes	1	Diesel	Generator	N/A
24 Nov 21	Sunny	OP4	10:45	21.1	0.5	SE	No	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP5	10:49	20.2	2.5	NE	Yes	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP6	10:53	21.3	1.6	Ν	No	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP7	10:56	21.6	2.9	Ν	No	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP8	11:01	22.1	1.9	Ν	No	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP9	11:05	22.4	0.5	NE	Yes	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP10	11:08	21.3	3	NE	Yes	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP1	15:15	24.9	0.7	Ν	Yes	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP2	15:18	24.6	2.3	S	No	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP3	15:23	26	0.6	Ν	Yes	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP4	15:26	26.2	1.6	Е	No	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP5	15:30	23.9	2.5	Е	No	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP6	15:34	23.1	2.3	NE	Yes	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP7	15:38	25.4	1.8	S	No	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP8	15:41	25.7	0.5	SE	Yes	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP9	15:45	23.4	2.6	Ν	No	0	N/A	N/A	N/A
24 Nov 21	Sunny	OP10	15:49	23	2.6	NE	No	0	N/A	N/A	N/A
24 Nov 21	Fine	OP1	18:06	21.4	0.2	Ν	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
24 Nov 21	Fine	OP2	18:09	20.3	0.8	Ν	Yes	0	N/A	N/A	N/A
24 Nov 21	Fine	OP3	18:13	18.9	0.7	NE	No	0	N/A	N/A	N/A
24 Nov 21	Fine	OP4	18:16	19	0.9	Ν	Yes	0	N/A	N/A	N/A
24 Nov 21	Fine	OP5	18:20	19.6	1.3	S	No	0	N/A	N/A	N/A
24 Nov 21	Fine	OP6	18:23	19.7	1	Ν	No	0	N/A	N/A	N/A
24 Nov 21	Fine	OP7	18:26	19.6	0.5	NW	No	0	N/A	N/A	N/A
24 Nov 21	Fine	OP8	18:30	19.4	0.5	NW	No	0	N/A	N/A	N/A
24 Nov 21	Fine	OP9	18:34	19.2	0.8	NW	No	0	N/A	N/A	N/A
24 Nov 21	Fine	OP10	18:38	19.2	0.5	NW	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP1	10:41	25.7	1.5	NE	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP2	10:45	28.1	0.9	NE	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP3	10:49	30	0.5	NE	No	1	Diesel	Generator	N/A
25 Nov 21	Sunny	OP4	10:52	31.2	1	Ν	Yes	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP5	10:56	30.5	1	NE	Yes	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP6	10:59	27.7	2.4	Ν	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP7	11:04	27.3	1.9	Ν	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP8	11:08	27.1	1.7	Ν	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP9	11:12	27.8	1.1	Ν	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP10	11:16	30	0.5	Ν	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP1	14:33	24.9	3.2	S	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP2	14:37	25.2	2.2	S	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP3	14:41	27.3	1.3	SE	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP4	14:44	27.3	0.8	Ν	Yes	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP5	14:47	28.2	2	S	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP6	14:50	27.1	2.2	S	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP7	14:54	26.7	2.6	S	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP8	14:58	26.6	2.6	S	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP9	15:02	26.9	2	SW	No	0	N/A	N/A	N/A
25 Nov 21	Sunny	OP10	15:05	27.7	2.1	S	No	0	N/A	N/A	N/A
25 Nov 21	Fine	OP1	18:06	24.4	0.8	S	No	0	N/A	N/A	N/A
25 Nov 21	Fine	OP2	18:10	26.1	0.5	S	No	0	N/A	N/A	N/A
25 Nov 21	Fine	OP3	18:14	25.3	0.4	S	No	0	N/A	N/A	N/A
25 Nov 21	Fine	OP4	18:19	25	0.8	Е	No	0	N/A	N/A	N/A
25 Nov 21	Fine	OP5	18:23	25.2	0.6	S	No	0	N/A	N/A	N/A
25 Nov 21	Fine	OP6	18:26	25.7	0.9	Ν	No	0	N/A	N/A	N/A
25 Nov 21	Fine	OP7	18:30	25.1	1.3	Ν	No	0	N/A	N/A	N/A
25 Nov 21	Fine	OP8	18:35	25.7	1.6	Ν	No	0	N/A	N/A	N/A
25 Nov 21	Fine	OP9	18:40	24.8	0.7	Ν	No	1	Acidic	Town gas plant	Intermittent

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
25 Nov 21	Fine	OP10	18:45	25.3	0.5	NE	Yes	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP1	10:33	30.1	0.6	Ν	Yes	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP2	10:38	30.3	0.7	S	No	0	Diesel	Generator	N/A
26 Nov 21	Sunny	OP3	10:47	30.6	0.6	S	No	1	Acidic	Leachate Treatment Plant	
26 Nov 21	Sunny	OP4	10:53	29	0.9	S	No	1	N/A	N/A	N/A
26 Nov 21	Sunny	OP5	10:58	29.5	0.7	NE	Yes	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP6	11:02	28	2.1	NW	No	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP7	11:06	28.3	2.1	Ν	No	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP8	11:10	28	2.2	Ν	No	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP9	11:14	27.9	1.7	Ν	No	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP10	11:17	27.5	2.7	Ν	No	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP1	14:47	24.5	3.1	Ν	Yes	1	Grass	Ground	N/A
26 Nov 21	Sunny	OP2	14:51	27.1	1.1	Ν	Yes	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP3	14:54	25.7	0.8	NW	Yes	1	Diesel	Generator	N/A
26 Nov 21	Sunny	OP4	14:57	25.3	0.9	NW	Yes	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP5	15:01	27.5	1.1	Ν	No	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP6	15:04	26.7	1.7	NE	Yes	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP7	15:07	25.9	1.8	Ν	No	0	N/A	N/A	N/A
26 Nov 21	Sunny	OP8	15:11	27.4	1.8	Ν	No	1	Diesel	Generator	N/A
26 Nov 21	Sunny	OP9	15:16	24.4	3.1	Ν	No	1	Town gas	Town gas plant	N/A
26 Nov 21	Sunny	OP10	15:18	24.2	2.4	NE	Yes	0	N/A	N/A	N/A
26 Nov 21	Fine	OP1	18:19	22.2	2.1	S	No	0	N/A	N/A	N/A
26 Nov 21	Fine	OP2	18:22	22.1	0.2	S	No	0	N/A	N/A	N/A
26 Nov 21	Fine	OP3	18:26	22.1	1.2	SE	No	0	N/A	N/A	N/A
26 Nov 21	Fine	OP4	18:29	22.3	0.8	NE	Yes	0	N/A	N/A	N/A
26 Nov 21	Fine	OP5	18:33	22.3	3.6	Е	No	0	N/A	N/A	N/A
26 Nov 21	Fine	OP6	18:36	22.5	1.8	NE	Yes	0	N/A	N/A	N/A
26 Nov 21	Fine	OP7	18:40	22.5	1.3	NE	Yes	0	N/A	N/A	N/A
26 Nov 21	Fine	OP8	18:43	22.6	0.9	Е	Yes	0	N/A	N/A	N/A
26 Nov 21	Fine	OP9	18:46	22.5	0.7	Ν	No	0	N/A	N/A	N/A
26 Nov 21	Fine	OP10	18:49	22.6	1.2	NW	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP1	10:38	27	1.8	NE	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP2	10:43	30.3	0.8	Ν	Yes	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP3	10:47	29.6	2.2	SW	No	1	Diesel	Generator	N/A
27 Nov 21	Sunny	OP4	10:51	29.7	1.2	Е	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP5	10:55	28.3	2.2	Е	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP6	10:58	28.7	1.3	S	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP7	11:01	28.3	1.4	Ν	No	1	Diesel	Generator	N/A

Date	Weather	Location	Time	Temperature	_		From	Odour	Odour	Possible Source	Remarks
				(oC)	(m/s)	Direction	Project Site	5	Characteristic		
27 Nov 21	Sunny	OP8	11:05	27.7	1.8	N	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP9	11:09	27	3.5	N	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP10	11:12	27.2	2.1	SE	Yes	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP1	14:34	27.1	2.4	S	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP2	14:38	27.3	2.3	S	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP3	14:42	27.8	1.4	W	No	1	Diesel	Generator	N/A
27 Nov 21	Sunny	OP4	14:46	29.2	1.3	E	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP5	14:50	27.5	2.2	E	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP6	14:54	25.8	4.7	NE	Yes	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP7	14:58	28.3	2.4	S	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP8	15:02	29	0.9	E	Yes	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP9	15:07	28.1	3.1	Ν	No	0	N/A	N/A	N/A
27 Nov 21	Sunny	OP10	15:11	28.7	1.7	Ν	No	0	N/A	N/A	N/A
27 Nov 21	Fine	OP1	18:05	22.4	1.3	Ν	Yes	0	N/A	N/A	N/A
27 Nov 21	Fine	OP2	18:09	23.1	0.2	Ν	Yes	0	N/A	N/A	N/A
27 Nov 21	Fine	OP3	18:13	22.9	0.7	S	No	0	N/A	N/A	N/A
27 Nov 21	Fine	OP4	18:17	23.8	1.2	S	No	0	N/A	N/A	N/A
27 Nov 21	Fine	OP5	18:21	23.5	1.9	Е	No	0	N/A	N/A	N/A
27 Nov 21	Fine	OP6	18:25	23.7	1.6	NE	Yes	0	N/A	N/A	N/A
27 Nov 21	Fine	OP7	18:29	24.1	0.4	Ν	No	0	N/A	N/A	N/A
27 Nov 21	Fine	OP8	18:33	25.2	1.4	SE	Yes	0	N/A	N/A	N/A
27 Nov 21	Fine	OP9	18:37	24.5	0.7	Ν	No	0	N/A	N/A	N/A
27 Nov 21	Fine	OP10	18:42	24.3	0.7	Ν	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP1	10:36	29.7	0.8	Ν	Yes	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP2	10:40	28.3	2.2	S	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP3	10:44	27	2.3	S	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP4	10:47	28.3	2.5	Е	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP5	10:51	26.3	3.2	Е	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP6	10:55	26.5	3.4	S	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP7	10:58	28.6	1.3	Ν	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP8	11:03	27.1	3.8	Ν	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP9	11:07	27.2	3.3	N	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP10	11:11	27.1	2.7	N	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP1	15:40	30.1	0.6	S	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP2	15:35	28.5	2.3	S	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP3	15:31	31.2	0.5	NE	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP4	15:28	30	0.8	E	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP5	15:24	27.3	3.2	E	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
28 Nov 21	Sunny	OP6	15:21	28.1	3.2	NE	Yes	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP7	15:17	31.3	0.9	NE	Yes	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP8	15:13	30.5	0.9	E	Yes	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP9	15:09	29.6	3.4	N	No	0	N/A	N/A	N/A
28 Nov 21	Sunny	OP10	15:05	29.2	3	E	Yes	0	N/A	N/A	N/A
28 Nov 21	Fine	OP1	18:10	27.5	0.4	N	Yes	0	N/A	N/A	N/A
28 Nov 21	Fine	OP2	18:14	26.3	0.4	N	Yes	0	N/A	N/A	N/A
28 Nov 21	Fine	OP3	18:18	26.6	0.4	E	No	0	N/A	N/A	N/A
28 Nov 21	Fine	OP4	18:23	26.7	1.2	W	No	0	N/A	N/A	N/A
28 Nov 21	Fine	OP5	18:27	27.5	0.6	E	No	0	N/A	N/A	N/A
28 Nov 21	Fine	OP6	18:31	26.4	2.1	N	No	0	N/A	N/A	N/A
28 Nov 21	Fine	OP7	18:35	27.4	1.3	NE	Yes	0	N/A	N/A	N/A
28 Nov 21	Fine	OP8	18:39	27.1	0.9	N	No	0	N/A	N/A	N/A
28 Nov 21	Fine	OP9	18:42	27.3	0.7	N	No	1	Acidic	Town gas plant	N/A
28 Nov 21	Fine	OP10	18:46	28.2	0.6	N	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP1	11:10	30.2	1.6	N	Yes	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP2	11:15	30.6	1.7	N	Yes	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP3	11:20	29.8	1.1	NE	Yes	1	Diesel	Generator	N/A
29 Nov 21	Sunny	OP4	11:24	29.6	2.3	N	Yes	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP5	11:28	28.3	2.6	Е	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP6	11:32	29	2.7	NE	Yes	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP7	11:35	28.4	1.9	Ν	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP8	11:39	28.1	1.7	Ν	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP9	11:43	28.4	1.5	Ν	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP10	11:46	27.9	2.4	Ν	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP1	14:33	28.5	0.4	Ν	Yes	1	Grass	Vegetation	N/A
29 Nov 21	Sunny	OP2	14:37	28.1	0.9	Е	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP3	14:41	28.5	1.4	NE	Yes	1	Diesel	Generator	N/A
29 Nov 21	Sunny	OP4	14:44	27.8	1.3	Е	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP5	14:48	28.6	1.5	Ν	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP6	14:50	29.1	0	N/A	N/A	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP7	14:54	28.6	0.5	N	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP8	14:57	28.4	0.5	Ν	No	0	N/A	N/A	N/A
29 Nov 21	Sunny	OP9	15:01	28.6	1	Ν	No	1	Acidic fume	Town gas plant	N/A
29 Nov 21	Sunny	OP10	15:04	29.4	0.6	NE	Yes	0	N/A	N/A	N/A
29 Nov 21	Fine	OP1	18:09	22	0	N/A	N/A	0	N/A	N/A	N/A
29 Nov 21	Fine	OP2	18:13	22.2	0	N/A	N/A	0	N/A	N/A	N/A
29 Nov 21	Fine	OP3	18:18	21.8	0.2	Ń	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
29 Nov 21	Fine	OP4	18:22	22.7	0.3	S	No	0	N/A	N/A	N/A
29 Nov 21	Fine	OP5	18:26	23	0.2	S	No	0	N/A	N/A	N/A
29 Nov 21	Fine	OP6	18:29	23.2	0.4	S	No	0	N/A	N/A	N/A
29 Nov 21	Fine	OP7	18:34	23.3	0	N/A	N/A	0	N/A	N/A	N/A
29 Nov 21	Fine	OP8	18:37	22.3	1.9	Ń	No	0	N/A	N/A	N/A
29 Nov 21	Fine	OP9	18:41	22.4	1	Ν	No	1	Acidic	, Town gas plant	N/A
29 Nov 21	Fine	OP10	18:46	22.7	0.2	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP1	10:33	24.1	3.7	Ν	Yes	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP2	10:36	24.5	4.1	Ν	Yes	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP3	10:40	25.5	2.5	Ν	Yes	1	Diesel	Generator	N/A
30 Nov 21	Sunny	OP4	10:43	26.6	1.7	Ν	Yes	1	Acidic	Leachate Treatment Plant	
30 Nov 21	Sunny	OP5	10:46	26.7	4.4	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP6	10:49	25.7	3.3	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP7	10:53	26.3	3.1	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP8	10:56	25.8	4.4	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP9	10:59	27.3	2.4	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP10	11:03	27.4	1.3	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP1	14:36	25.8	1.3	Ν	Yes	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP2	14:39	26.9	1.8	Ν	Yes	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP3	14:42	29.4	1.2	NE	Yes	1	Diesel	Generator	N/A
30 Nov 21	Sunny	OP4	14:46	29.4	0.7	Ν	Yes	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP5	14:50	29.3	2.1	Е	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP6	14:53	28.5	1.8	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP7	14:57	26.8	3.1	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP8	15:00	28.2	1.5	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP9	15:04	26.9	6.6	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Sunny	OP10	15:07	26.6	2.8	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Fine	OP1	18:00	22.3	3.1	Ν	Yes	0	N/A	N/A	N/A
30 Nov 21	Fine	OP2	18:03	21.9	3	Ν	Yes	0	N/A	N/A	N/A
30 Nov 21	Fine	OP3	18:07	22.1	2.4	Ν	Yes	0	N/A	N/A	N/A
30 Nov 21	Fine	OP4	18:10	22.5	0.8	NE	Yes	0	N/A	N/A	N/A
30 Nov 21	Fine	OP5	18:13	22.7	2.8	NE	Yes	0	N/A	N/A	N/A
30 Nov 21	Fine	OP6	18:16	21.7	3.4	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Fine	OP7	18:20	22.1	4.7	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Fine	OP8	18:23	21.4	5.6	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Fine	OP9	18:26	21.6	4.7	Ν	No	0	N/A	N/A	N/A
30 Nov 21	Fine	OP10	18:32	21.9	2.4	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP1	10:30	20	4.7	Ν	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature	_		From	Odour	Odour	Possible Source	Remarks
				(oC)	(m/s)	Direction	Project Site		Characteristic		
1-Dec-21	Sunny	OP2	10:33	20.6	3.9	Ν	Yes	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP3	10:37	22.5	1.2	Ν	Yes	1	Oil	Electric Generator	N/A
1-Dec-21	Sunny	OP4	10:40	22.7	2.3	Ε	No	1	Acidic	Leachate Treatment Plant	
1-Dec-21	Sunny	OP5	10:43	22.6	3.6	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP6	10:47	20.8	4.5	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP7	10:50	19.7	6.2	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP8	10:53	20.3	4.2	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP9	10:57	20.4	4.6	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP10	11:01	21.5	1.7	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP1	14:39	20.8	2.6	Ν	Yes	1	grassy	Vegetation	N/A
1-Dec-21	Sunny	OP2	14:43	22.1	0.8	NW	Yes	1	grassy	Vegetation	N/A
1-Dec-21	Sunny	OP3	14:47	21.6	1.9	NE	Yes	1	Diesel	Generator	N/A
1-Dec-21	Sunny	OP4	14:50	24	0.9	Ν	Yes	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP5	14:55	22.6	1.1	NE	Yes	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP6	14:58	21	2.9	NE	Yes	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP7	15:01	20.7	2.7	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP8	15:05	21	1.5	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP9	15:08	21.5	3	NE	Yes	0	N/A	N/A	N/A
1-Dec-21	Sunny	OP10	15:11	22	0.5	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Fine	OP1	18:05	17.1	12	Ν	Yes	0	N/A	N/A	N/A
1-Dec-21	Fine	OP2	18:08	17.6	10.1	Ν	Yes	0	N/A	N/A	N/A
1-Dec-21	Fine	OP3	18:12	17.5	1.9	NE	Yes	0	N/A	N/A	N/A
1-Dec-21	Fine	OP4	18:16	17.2	4.5	Е	No	0	N/A	N/A	N/A
1-Dec-21	Fine	OP5	18:20	17.3	8.6	Е	No	0	N/A	N/A	N/A
1-Dec-21	Fine	OP6	18:24	17.6	7.5	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Fine	OP7	18:28	17.2	10.7	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Fine	OP8	18:32	17	6.5	Ν	No	1	Diesel	Electric Generator	N/A
1-Dec-21	Fine	OP9	18:36	17.5	6.4	Ν	No	0	N/A	N/A	N/A
1-Dec-21	Fine	OP10	18:40	17.7	4.1	Ν	No	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP1	10:33	22.5	3.6	Ν	Yes	0	N/A	N/A	Ń/A
2-Dec-21	Sunny	OP2	10:37	23.5	2.4	Ν	Yes	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP3	10:40	24.8	1.1	N	Yes	1	Oil	Electric Generator	N/A
2-Dec-21	Sunny	OP4	10:44	24.5	0.8	N	Yes	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP5	10:48	24.6	2.2	NE	Yes	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP6	10:52	24.4	2.6	N	No	0	N/A	N/A	N/A
2-Dec-21 2-Dec-21	Sunny	OP7	10:52	22.8	3.2	N	No	0	N/A	N/A	N/A
2-Dec-21 2-Dec-21	Sunny	OP8	10:58	23.1	2.6	N	No	0	N/A	N/A	N/A
2-Dec-21 2-Dec-21	Sunny	OP9	10.58 11:02	24.2	1.6	N	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature	-		From Project Site	Odour Interesity	Odour Characteristic	Possible Source	Remarks
		0.010	11.04	(oC)	(m/s)	Direction	Project Site		Characteristic	<b>NT / 1</b>	27/1
2-Dec-21	Sunny	OP10	11:06	24.6	0.8	N	No	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP1	14:32	22.5	2.4	N	Yes	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP2	14:35	24.8	1.7	N	Yes	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP3	14:38	24.1	1.8	Ν	Yes	1	Oil	Generator	N/A
2-Dec-21	Sunny	OP4	14:41	26	1.1	Ν	Yes	1	Acidic	Leachate Treatment Plant	
2-Dec-21	Sunny	OP5	14:44	26.6	0.6	NE	Yes	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP6	14:47	25.5	1.5	Ν	No	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP7	14:50	24.2	2.3	Ν	No	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP8	14:53	23.8	2.9	Ν	No	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP9	14:56	23.8	2.2	Ν	No	0	N/A	N/A	N/A
2-Dec-21	Sunny	OP10	15:02	24	1.4	NE	Yes	0	N/A	N/A	N/A
2-Dec-21	Fine	OP1	18:28	19.7	0.5	S	No	0	N/A	N/A	N/A
2-Dec-21	Fine	OP2	18:33	19.3	0.5	S	No	0	N/A	N/A	N/A
2-Dec-21	Fine	OP3	18:37	17.4	0.8	NE	Yes	0	N/A	N/A	N/A
2-Dec-21	Fine	OP4	18:40	17.5	0.9	NE	Yes	0	N/A	N/A	N/A
2-Dec-21	Fine	OP5	18:44	17.2	1.3	NW	No	0	N/A	N/A	N/A
2-Dec-21	Fine	OP6	18:49	17.5	1.1	Ν	No	0	N/A	N/A	N/A
2-Dec-21	Fine	OP7	18:52	17.7	1.3	Ν	No	0	N/A	N/A	N/A
2-Dec-21	Fine	OP8	18:56	17.8	1.3	Ν	No	0	N/A	N/A	N/A
2-Dec-21	Fine	OP9	18:59	18	1	Ν	No	0	N/A	N/A	N/A
2-Dec-21	Fine	OP10	19:03	18	0.5	NE	Yes	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP1	10:40	19.2	4.9	NW	Yes	1	grassy	Vegetation	N/A
3-Dec-21	Sunny	OP2	10:44	20.7	2.5	NW	Yes	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP3	10:47	20.2	0.8	Ν	Yes	1	Diesel	Generator	N/A
3-Dec-21	Sunny	OP4	10:50	21.1	1.4	Ν	Yes	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP5	10:54	21.4	0.9	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP6	10:56	21	3.6	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP7	10:59	20.4	2.9	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP8	11:02	19.5	4.3	N	No	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP9	11:06	19.4	5.9	N	No	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP10	11:08	19.8	1.9	N	No	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP1	14:33	23.3	1.5	N	Yes	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP2	14:36	24.2	1.2	N	Yes	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP3	14:40	25.6	1.8	NE	Yes	1	Oil	Electric Generator	N/A
3-Dec-21	Sunny	OP4	14:44	26.9	2.2	NE	Yes	1	Acidic	Leachate Treatment Plant	-
3-Dec-21	Sunny	OP5	14:44	25.8	1.1	N	No	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP6	14:51	24.5	2.8	N	No	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP7	14:51 14:54	24.3	3	N	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
3-Dec-21	Sunny	OP8	14:57	24.3	1.4	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP9	15:00	24	1.5	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Sunny	OP10	15:04	24.8	1	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Fine	OP1	18:03	23.2	1.4	Ν	Yes	0	N/A	N/A	N/A
3-Dec-21	Fine	OP2	18:07	22.4	2.2	Ν	Yes	0	N/A	N/A	N/A
3-Dec-21	Fine	OP3	18:11	23.7	0.7	Ν	Yes	0	N/A	N/A	N/A
3-Dec-21	Fine	OP4	18:15	24.2	0.5	Ν	Yes	0	N/A	N/A	N/A
3-Dec-21	Fine	OP5	18:19	24.5	0.4	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Fine	OP6	18:22	23.9	1.2	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Fine	OP7	18:25	23.2	1.3	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Fine	OP8	18:28	22.6	1.3	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Fine	OP9	18:32	23.1	1.6	Ν	No	0	N/A	N/A	N/A
3-Dec-21	Fine	OP10	18:36	24.2	0.6	Ν	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP1	10:40	26.1	2.2	S	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP2	10:44	25.8	1.9	S	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP3	10:48	25.2	2.8	SW	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP4	10:52	24.6	3.4	Е	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP5	10:56	24.1	2.6	Е	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP6	11:00	23.9	3.6	Ν	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP7	11:04	24	4.2	Ν	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP8	11:08	23.4	1.2	S	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP9	11:12	26.3	2.1	S	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP10	11:16	25.8	2.9	Ν	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP1	14:36	24.9	1.3	Ν	Yes	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP2	14:40	25.3	2.6	S	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP3	14:44	25.8	3.3	SW	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP4	14:48	24.8	2.3	Е	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP5	14:52	23.3	4.6	Е	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP6	14:56	25.2	1.2	SE	Yes	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP7	15:00	26.1	2	SW	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP8	15:03	26.7	1.5	S	No	0	N/A	N/A	N/A
4-Dec-21	Sunny	OP9	15:08	27.6	1.2	Ν	No	1	Acidic	Town gas	N/A
4-Dec-21	Sunny	OP10	15:12	25.8	4.3	NE	Yes	0	N/A	N/A	N/A
4-Dec-21	Fine	OP1	18:05	20.1	1.1	Ν	Yes	0	N/A	N/A	N/A
4-Dec-21	Fine	OP2	18:08	19.7	0.7	SE	No	0	N/A	N/A	N/A
4-Dec-21	Fine	OP3	18:12	19.6	0.7	SE	No	0	N/A	N/A	N/A
4-Dec-21	Fine	OP4	18:16	19.5	1.2	SE	No	0	N/A	N/A	N/A
4-Dec-21	Fine	OP5	18:19	19.2	2.7	Е	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
4-Dec-21	Fine	OP6	18:22	19.4	1.9	E	Yes	0	N/A	N/A	N/A
4-Dec-21	Fine	OP7	18:25	19.7	1.2	Ν	No	0	N/A	N/A	N/A
4-Dec-21	Fine	OP8	18:28	19.5	0.8	NE	Yes	0	N/A	N/A	N/A
4-Dec-21	Fine	OP9	18:32	19.4	0.7	NE	Yes	1	Acidic	Town gas plant	Ň/A
4-Dec-21	Fine	OP10	18:36	19.6	0.6	NE	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP1	10:33	24.6	2.3	Ν	Yes	0	N/A	N/A	Ň/A
5-Dec-21	Sunny	OP2	10:37	26.1	0.7	Ν	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP3	10:40	26.3	1.2	Ν	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP4	10:44	26.1	0.9	Ν	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP5	10:49	25.6	2.5	NE	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP6	10:53	25.4	2.5	Ν	No	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP7	10:56	26.2	1.8	Ν	No	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP8	11:00	26.3	1.7	Ν	No	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP9	11:04	25.8	2.3	Ν	No	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP10	11:08	25.3	1.1	Ν	No	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP1	15:15	26.3	2.5	NE	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP2	15:18	26.9	1.6	NE	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP3	15:21	27.1	2.2	NE	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP4	15:25	27.2	1.7	Ν	No	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP5	15:30	26.5	2.7	SE	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP6	15:34	26.3	1.8	Е	No	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP7	15:39	25.1	4.2	Е	No	1	Acidic	Leachate Treatment Plant	N/A
5-Dec-21	Sunny	OP8	15:43	26.4	1.7	NW	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP9	15:47	26.9	1.2	SW	Yes	0	N/A	N/A	N/A
5-Dec-21	Sunny	OP10	15:51	26.2	0.5	S	No	0	N/A	N/A	N/A
5-Dec-21	Fine	OP1	18:00	21.3	0.6	Ν	Yes	0	N/A	N/A	N/A
5-Dec-21	Fine	OP2	18:04	22.2	0.4	S	No	0	N/A	N/A	N/A
5-Dec-21	Fine	OP3	18:07	22.4	0.6	Ν	Yes	0	N/A	N/A	N/A
5-Dec-21	Fine	OP4	18:11	22.1	1.3	Е	No	1	Acidic	Leachate Treatment Plant	N/A
5-Dec-21	Fine	OP5	18:14	21.8	1.9	Е	No	0	N/A	N/A	N/A
5-Dec-21	Fine	OP6	18:17	22.3	0.9	Ν	No	0	N/A	N/A	N/A
5-Dec-21	Fine	OP7	18:20	22.5	0.7	Ν	No	0	N/A	N/A	N/A
5-Dec-21	Fine	OP8	18:24	21.6	1.4	Ν	No	0	N/A	N/A	N/A
5-Dec-21	Fine	OP9	18:31	22.1	0.8	Ν	No	0	N/A	N/A	N/A
5-Dec-21	Fine	OP10	18:36	22.4	1.5	Ν	No	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP1	10:35	24.1	3.3	Ν	Yes	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP2	10:39	26	1.4	Ν	Yes	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP3	10:44	26.1	1.9	Ν	Yes	1	Oil	Generator	N/A

Date	Weather	Location	Time	Temperature (oC)	-	Wind Direction	From Project Site	Odour Intonsity	Odour Characteristic	Possible Source	Remarks
( D 01	C	OD4	10.40	· · /	(m/s)					NT / A	
6-Dec-21	Sunny	OP4 OP5	10:49	25.8 25.6	2.2 0.9	NE NE	Yes	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP5 OP6	10:53 10:57	25.6 25.4			Yes	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP6 OP7	10:57 11:00		1.2	N	No No	0	N/A	N/A	N/A
6-Dec-21	Sunny			24.3	1.1	N		0	N/A	N/A	N/A
6-Dec-21	Sunny	OP8	11:04	24.8	0.7	N	No	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP9	11:08	25.6	1	SE	Yes	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP10	11:12	24.8	0.8	E	Yes	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP1	14:34	24.1	1.4	N	Yes	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP2	14:37	23.2	2.1	NW	Yes	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP3	14:40	25.8	1.1	N	Yes	1	Diesel	Generator	N/A
6-Dec-21	Sunny	OP4	14:44	24.4	2.5	E	No	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP5	14:47	23.7	2.4	E	No	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP6	14:50	25.7	0.8	NE	Yes	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP7	14:53	24.8	1.8	Ν	No	1	Wood Material	Worksite Constructing	N/A
6-Dec-21	Sunny	OP8	14:58	25.8	1.8	Ν	No	0	N/A	N/A	N/A
6-Dec-21	Sunny	OP9	15:03	27.2	0.4	NE	Yes	1	Town gas	Town gas plant	N/A
6-Dec-21	Sunny	OP10	15:06	23.9	1.2	Ν	No	0	N/A	N/A	N/A
6-Dec-21	Fine	OP1	18:10	25.8	0.6	Ν	Yes	0	N/A	N/A	N/A
6-Dec-21	Fine	OP2	18:14	25.4	0.7	Ν	Yes	0	N/A	N/A	N/A
6-Dec-21	Fine	OP3	18:18	25.5	0.5	E	No	0	N/A	N/A	N/A
6-Dec-21	Fine	OP4	18:21	25.3	1.3	Е	No	0	N/A	N/A	N/A
6-Dec-21	Fine	OP5	18:25	25.6	1.6	E	No	0	N/A	N/A	N/A
6-Dec-21	Fine	OP6	18:28	25.6	0.7	Ν	No	0	N/A	N/A	N/A
6-Dec-21	Fine	OP7	18:33	25.2	1.4	Ν	No	0	N/A	N/A	N/A
6-Dec-21	Fine	OP8	18:37	25.5	0.5	Ν	No	0	N/A	N/A	N/A
6-Dec-21	Fine	OP9	18:41	25.7	0.5	Ν	No	0	N/A	N/A	N/A
6-Dec-21	Fine	OP10	18:45	24.9	0.6	Ν	No	0	N/A	N/A	N/A
7-Dec-21	Sunny	OP1	10:33	26.3	1.4	Ν	Yes	0	N/A	N/A	N/A
7-Dec-21	Sunny	OP2	10:37	26.1	3.1	Ν	Yes	0	N/A	N/A	N/A
7-Dec-21	Sunny	OP3	10:40	27.1	0.6	S	No	1	Oil	Electric Generator	N/A
7-Dec-21	Sunny	OP4	10:44	26.6	0.7	Е	No	0	N/A	N/A	N/A
7-Dec-21	Sunny	OP5	10:49	25.9	2.5	Е	No	0	N/A	N/A	N/A
7-Dec-21	Sunny	OP6	10:54	25.6	1.8	Ν	No	0	N/A	N/A	N/A
7-Dec-21	Sunny	OP7	10:58	26.4	1.7	N	No	0	N/A	N/A	N/A
7-Dec-21	Sunny	OP8	11:03	26.1	1.2	N	No	1	Oil	Electric Generator	N/A
7-Dec-21	Sunny	OP9	11:07	26.3	1.8	N	No	0	N/A	N/A	N/A
7-Dec-21	Sunny	OP10	11:11	26.8	1.4	N	No	0	N/A	N/A	N/A
7-Dec-21	Overcast	OP1	14:39	23.9	0.6	NE	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
7-Dec-21	Overcast	OP2	14:41	23.3	3.2	S	No	0	N/A	N/A	N/A
7-Dec-21	Overcast	OP3	14:44	23.6	0.6	N	Yes	0	N/A	N/A	N/A
7-Dec-21	Overcast	OP4	14:47	23.5	1.2	Е	No	0	N/A	N/A	Ň/A
7-Dec-21	Overcast	OP5	14:51	23.2	2.3	NE	Yes	0	, N/A	N/A	Ň/A
7-Dec-21	Overcast	OP6	14:53	22.9	3.3	Е	Yes	0	N/A	N/A	N/A
7-Dec-21	Overcast	OP7	14:56	23.7	2.2	S	No	0	N/A	N/A	N/A
7-Dec-21	Overcast	OP8	14:59	24.2	1.2	S	No	0	N/A	N/A	Ň/A
7-Dec-21	Overcast	OP9	15:02	24.5	2.7	NE	Yes	0	N/A	N/A	N/A
7-Dec-21	Overcast	OP10	15:06	24.3	2.2	NE	Yes	0	N/A	N/A	N/A
7-Dec-21	Fine	OP1	18:37	24.8	1.6	Ν	Yes	0	N/A	N/A	N/A
7-Dec-21	Fine	OP2	18:41	24.6	1.9	Ν	Yes	0	N/A	N/A	Ň/A
7-Dec-21	Fine	OP3	18:45	24.5	2	W	No	0	N/A	N/A	N/A
7-Dec-21	Fine	OP4	18:49	23.9	1.3	W	No	0	N/A	N/A	N/A
7-Dec-21	Fine	OP5	18:53	24.2	2.5	NE	Yes	0	N/A	N/A	Ň/A
7-Dec-21	Fine	OP6	18:56	24.9	0.9	NE	Yes	0	N/A	N/A	N/A
7-Dec-21	Fine	OP7	19:00	25.4	1.3	S	No	0	N/A	N/A	N/A
7-Dec-21	Fine	OP8	19:04	25.2	0.7	S	No	1	Oil	Electric Generator	Ň/A
7-Dec-21	Fine	OP9	19:07	24.9	3.1	S	No	0	N/A	N/A	Ň/A
7-Dec-21	Fine	OP10	19:11	24.5	0.9	S	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP1	10:37	25.6	0.4	NW	Yes	1	grassy	Vegetation	N/A
8-Dec-21	Sunny	OP2	10:40	23.6	2.3	S	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP3	10:43	22.4	2.6	W	No	1	Diesel	Generator	N/A
8-Dec-21	Sunny	OP4	10:46	23.1	2.3	W	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP5	10:50	21.1	6.5	NE	Yes	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP6	10:52	22.2	2.7	Ν	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP7	10:55	22.4	1.9	S	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP8	10:59	22.9	1.1	Ν	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP9	11:02	23.2	1.7	S	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP10	11:05	22.8	1.4	Ν	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP1	14:32	25.9	1.3	NW	Yes	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP2	14:36	26.1	1.6	SE	Yes	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP3	14:40	25.9	2.1	NW	Yes	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP4	14:43	26.9	1.6	W	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP5	14:47	25.8	2.7	NE	Yes	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP6	14:50	25.3	1.8	SW	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP7	14:54	25.8	1.2	NW	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP8	14:57	26.1	1	S	No	0	N/A	N/A	N/A
8-Dec-21	Sunny	OP9	15:01	25.3	2.7	E	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
8-Dec-21	Sunny	OP10	15:05	25.2	0.9	N	No	0	N/A	N/A	N/A
8-Dec-21	Fine	OP1	18:10	24.3	1.9	Ν	Yes	0	N/A	N/A	N/A
8-Dec-21	Fine	OP2	18:14	24.6	2.6	Ν	Yes	0	N/A	N/A	N/A
8-Dec-21	Fine	OP3	18:20	24.1	0.9	W	No	0	, N/A	N/A	N/A
8-Dec-21	Fine	OP4	18:25	24.3	0.7	Е	No	0	N/A	N/A	N/A
8-Dec-21	Fine	OP5	18:31	24.4	1.5	NW	No	0	N/A	N/A	N/A
8-Dec-21	Fine	OP6	18:35	23.9	2	Ν	No	0	N/A	N/A	N/A
8-Dec-21	Fine	OP7	18:41	24.7	1.6	Ν	No	0	N/A	N/A	N/A
8-Dec-21	Fine	OP8	18:44	24.2	2.5	S	No	0	N/A	N/A	N/A
8-Dec-21	Fine	OP9	18:48	23.3	3.4	NE	Yes	0	N/A	N/A	N/A
8-Dec-21	Fine	OP10	18:53	23.2	2.3	NE	Yes	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP1	10:35	27.1	0.6	S	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP2	10:39	27.2	0.7	S	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP3	10:43	24.9	3.2	W	No	1	Oil	Electric Generator	N/A
9-Dec-21	Sunny	OP4	10:47	25.3	1.3	Е	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP5	10:51	24.4	2.9	NE	Yes	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP6	10:55	25.4	2.3	S	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP7	10:58	27.2	1.2	Ν	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP8	11:00	25.5	1.8	Ν	No	1	Acidic Gas	Town Gas Plant	N/A
9-Dec-21	Sunny	OP9	11:04	25.4	0.7	NE	Yes	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP10	11:07	25.1	2.2	NE	Yes	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP1	14:40	25.4	0.6	S	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP2	14:45	25.5	1.6	S	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP3	14:49	25.2	1.1	S	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP4	14:53	25.4	0.9	Е	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP5	14:57	27.3	0.7	E	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP6	15:00	26.2	0.5	Ν	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP7	15:04	26.6	1.6	S	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP8	15:07	25.4	1.5	Ν	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP9	15:10	25.2	2.8	Ν	No	0	N/A	N/A	N/A
9-Dec-21	Sunny	OP10	15:13	24.6	1.5	E	Yes	0	N/A	N/A	N/A
9-Dec-21	Fine	OP1	18:03	26.1	0.5	Ν	Yes	0	N/A	N/A	N/A
9-Dec-21	Fine	OP2	18:07	25.8	0.5	S	No	0	N/A	N/A	N/A
9-Dec-21	Fine	OP3	18:11	25.6	0.4	Е	No	0	N/A	N/A	N/A
9-Dec-21	Fine	OP4	18:15	24.7	1.1	SE	No	0	N/A	N/A	N/A
9-Dec-21	Fine	OP5	18:20	25.1	1.8	Е	No	0	N/A	N/A	N/A
9-Dec-21	Fine	OP6	18:24	25.4	0.6	Ν	No	0	N/A	N/A	N/A
9-Dec-21	Fine	OP7	18:29	24.8	0.5	Ν	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
9-Dec-21	Fine	OP8	18:32	25.2	0.7	N	No	1	Acidic Gas	Town gas plant	N/A
9-Dec-21	Fine	OP9	18:36	25.9	0.2	N	No	1	Town gas	Town gas plant	N/A
9-Dec-21	Fine	OP10	18:40	24.8	1.1	N	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP1	10:39	23.1	2.9	N	Yes	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP2	10:42	24.3	1.6	SW	Yes	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP3	10:44	24.5	1.3	SW	No	1	Diesel	Generator	N/A
10-Dec-21	Sunny	OP4	10:47	23.4	1.3	NE	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP5	10:50	24.5	1.3	NE	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP6	10:52	23.9	1.8	NW	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP7	10:54	24.4	2.3	NW	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP8	10:58	24.8	1.6	NW	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP9	11:03	24.4	3.7	NW	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP10	11:05	24.6	1.1	SE	Yes	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP11	11:12	24.3	2.2	S	Yes	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP1	14:35	26.3	1.4	S	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP2	14:39	26.5	0.8	S	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP3	14:43	26.1	1.4	SW	No	1	Oil	Generator	N/A
10-Dec-21	Sunny	OP4	14:48	26.3	2.4	Е	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP5	14:50	25.3	3.1	Е	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP6	14:54	26.1	0.8	S	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP7	14:57	25.8	1.8	Ν	Yes	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP8	15:01	24.6	3.3	Ν	Yes	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP9	15:05	27	1.2	SW	No	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP10	15:09	26.7	0.9	Е	Yes	0	N/A	N/A	N/A
10-Dec-21	Sunny	OP11	15:21	27.4	2.7	Е	No	0	N/A	N/A	N/A
10-Dec-21	Fine	OP1	18:05	24.9	1.8	S	No	0	N/A	N/A	N/A
10-Dec-21	Fine	OP2	18:09	25.1	0.6	S	No	0	N/A	N/A	N/A
10-Dec-21	Fine	OP3	18:13	24.6	0.8	W	No	0	N/A	N/A	N/A
10-Dec-21	Fine	OP4	18:17	24.4	4.2	Е	No	0	N/A	N/A	N/A
10-Dec-21	Fine	OP5	18:20	24	3.4	Е	No	0	N/A	N/A	N/A
10-Dec-21	Fine	OP6	18:23	24.2	2.9	Ν	No	0	N/A	N/A	N/A
10-Dec-21	Fine	OP7	18:27	24.8	0.8	Ν	Yes	0	N/A	N/A	N/A
10-Dec-21	Fine	OP8	18:30	25.3	2.7	S	No	0	N/A	N/A	N/A
10-Dec-21	Fine	OP9	18:34	25.1	0.8	Ν	No	0	N/A	N/A	N/A
10-Dec-21	Fine	OP10	18:38	24.9	1.3	Ν	No	0	N/A	N/A	Ň/A
10-Dec-21	Fine	OP11	18:48	24.7	0.7	W	Yes	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP1	10:35	27.4	1.1	Ν	Yes	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP2	10:38	28.1	0.7	N	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature	-		From	Odour	Odour Chanadariatia	Possible Source	Remarks
44 D 04		0.00	10.11	(oC)	(m/s)	Direction	Project Site		Characteristic	27/4	<b>NT / A</b>
11-Dec-21	Sunny	OP3	10:41	28.2	1.9	NE	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP4	10:45	27.1	3.2	NE	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP5	10:49	27.3	2.9	E	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP6	10:53	27.4	2.6	Е	Yes	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP7	10:57	28.3	0.9	S	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP8	11:00	28.5	0.4	S	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP9	11:04	28.0	2.2	NE	Yes	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP10	11:07	27.6	3.2	Ν	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP11	11:20	28.8	1.8	Е	No	1	Oil	Generator	N/A
11-Dec-21	Sunny	OP1	15:04	28.7	0.6	SW	Yes	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP2	15:08	26.4	2.3	S	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP3	15:12	26.2	1.3	S	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP4	15:15	27.4	1.2	NE	Yes	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP5	15:19	26.4	2.6	Е	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP6	15:23	27.1	1.3	Е	Yes	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP7	15:27	28.5	0.6	SW	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP8	15:31	27.6	0.7	SE	Yes	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP9	15:34	28.1	1.3	S	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP10	15:38	26.1	2.9	S	No	0	N/A	N/A	N/A
11-Dec-21	Sunny	OP11	15:50	26.2	3.3	SE	No	0	N/A	N/A	N/A
11-Dec-21	Fine	OP1	18:06	23.0	0.1	Ν	Yes	0	N/A	N/A	N/A
11-Dec-21	Fine	OP2	18:10	22.4	0.6	Ν	Yes	0	N/A	N/A	N/A
11-Dec-21	Fine	OP3	18:13	22.3	0.5	Е	No	0	N/A	N/A	N/A
11-Dec-21	Fine	OP4	18:17	22.2	0.8	SE	No	0	N/A	N/A	N/A
11-Dec-21	Fine	OP5	18:21	22.1	1.9	NE	Yes	0	N/A	N/A	N/A
11-Dec-21	Fine	OP6	18:24	21.9	1.0	NE	Yes	0	N/A	N/A	N/A
11-Dec-21	Fine	OP7	18:27	21.9	0.7	N	No	0	N/A	N/A	N/A
11-Dec-21	Fine	OP8	18:31	21.0	1.1	N	No	0	N/A	N/A	N/A
11-Dec-21	Fine	OP9	18:34	20.9	1.8	N	No	0	N/A	N/A	N/A
11-Dec-21	Fine	OP10	18:37	21.4	0.6	NE	Yes	0	N/A	N/A	N/A
11-Dec-21	Fine	OP11 OP11	18:45	22.6	1.1	NE	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP1	10:45	27.2	1.1	N	Yes	0	N/A	N/A	N/A
12-Dec-21 12-Dec-21	Sunny	OP2	10:35	26.5	2.2	N	Yes	0	N/A	N/A	N/A
12-Dec-21 12-Dec-21	Sunny	OP3	10:40	26.3	1.8	SW	No	0	N/A	N/A N/A	N/A N/A
12-Dec-21 12-Dec-21	5	OP4	10:43	26.1	3.5	E	No	0	N/A	N/A N/A	N/A
12-Dec-21 12-Dec-21	Sunny Sunny	OP4 OP5	10:47	25.3	2.2	E	No	0	N/A	N/A N/A	N/A
12-Dec-21 12-Dec-21	5	OP5 OP6	10:51	25.5 25.5	1.1	E S	No		N/A N/A	N/A N/A	N/A N/A
	Sunny	OP6 OP7		25.5 24.9		S S		0 0		-	
12-Dec-21	Sunny	UP/	10:59	24.9	1.3	5	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
12-Dec-21	Sunny	OP8	11:03	25.2	1.1	Ν	Yes	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP9	11:08	24.8	2.4	Ν	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP10	11:10	24.5	0.9	Е	Yes	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP11	11:18	24.4	3.2	Е	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP1	15:46	24.4	3.1	S	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP2	15:41	24.5	0.7	S	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP3	15:37	24.7	0.8	SW	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP4	15:34	24.8	1.2	S	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP5	15:31	25.0	1.6	S	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP6	15:27	24.7	1.8	S	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP7	15:24	25.1	2.7	S	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP8	15:19	25.7	1.7	S	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP9	15:14	26.1	2.2	S	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP10	15:10	25.3	1.1	S	No	0	N/A	N/A	N/A
12-Dec-21	Sunny	OP11	15:01	25.5	2.5	Е	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP1	18:02	24.2	1.0	S	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP2	18:06	24.0	0.4	S	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP3	18:10	23.7	0.6	S	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP4	18:13	23.5	1.7	Е	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP5	18:17	23.6	1.3	Е	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP6	18:21	23.8	1.5	S	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP7	18:26	23.6	1.9	S	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP8	18:30	24.1	0.5	S	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP9	18:34	24.3	0.7	Ν	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP10	18:37	24.5	0.6	Ν	No	0	N/A	N/A	N/A
12-Dec-21	Fine	OP11	18:50	24.3	0.8	Е	No	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP1	10:46	21.0	2.4	Ν	Yes	1	Grassy	Vegetation	N/A
13-Dec-21	Sunny	OP2	10:50	21.1	2.1	Ν	Yes	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP3	10:53	23.4	0.8	Ν	Yes	1	Diesel	Generator	N/A
13-Dec-21	Sunny	OP4	10:55	22.2	1.6	NE	Yes	1	Leachate	Leachate Treatment Plant	N/A
13-Dec-21	Sunny	OP5	10:59	20.8	3.9	Е	No	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP6	11:01	20.1	4.8	NE	Yes	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP7	11:04	21.3	4.4	NE	Yes	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP8	11:07	20.6	2.2	NE	Yes	1	Diesel	Generator	N/A
13-Dec-21	Sunny	OP9	11:11	20.2	2.2	NE	Yes	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP10	11:13	21.0	1.6	NE	Yes	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP11	11:30	22.3	1.6	S	Yes	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP1	14:35	24.3	1.3	S	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
13-Dec-21	Sunny	OP2	14:40	24.5	1.5	S	No	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP3	14:40	24.7	1.5	SW	No	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP4	14:49	24.9	1.7	E	No	1	Acidic	Slurry Truck	N/A
13-Dec-21	Sunny	OP5	14:53	25.3	1.2	E	No	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP6	14:56	24.0	2.4	NE	Yes	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP7	15:00	25.4	0.8	NW	No	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP8	15:04	25.2	1.1	N	Yes	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP9	15:07	24.5	2.0	N	No	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP10	15:10	24.7	0.9	NE	Yes	0	N/A	N/A	N/A
13-Dec-21	Sunny	OP11	15:20	23.6	1.6	E	No	0	N/A	N/A	N/A
13-Dec-21	Fine	OP1	18:07	23.2	0.5	S	No	0	N/A	N/A	N/A
13-Dec-21	Fine	OP2	18:11	22.8	0.3	S	No	0	N/A	N/A	N/A
13-Dec-21	Fine	OP3	18:15	22.5	0.2	SE	No	0	N/A	N/A	N/A
13-Dec-21	Fine	OP4	18:19	22.6	0.7	E	No	0	N/A	N/A	N/A
13-Dec-21	Fine	OP5	18:22	22.5	1.3	W	No	0	N/A	N/A	N/A
13-Dec-21	Fine	OP6	18:25	22.4	0.8	S	No	0	N/A	N/A	N/A
13-Dec-21	Fine	OP7	18:29	22.1	0.8	N	Yes	0	N/A	N/A	N/A
13-Dec-21	Fine	OP8	18:33	22.3	0.7	N	Yes	0	N/A	N/A	N/A
13-Dec-21	Fine	OP9	18:36	22.5	0.6	S	No	0	N/A	N/A	N/A
13-Dec-21	Fine	OP10	18:40	22.2	0.5	Ν	No	0	N/A	N/A	N/A
13-Dec-21	Fine	OP11	18:49	22.6	0.5	Ν	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP1	10:35	24.4	2.1	Ν	Yes	0	N/A	N/A	Ň/A
14-Dec-21	Sunny	OP2	10:38	24.1	1.3	Ν	Yes	0	N/A	N/A	Ň/A
14-Dec-21	Sunny	OP3	10:42	24.5	0.6	S	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP4	10:45	24.2	0.5	S	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP5	10:49	24.3	1.7	Е	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP6	10:52	24.8	0.4	Ν	Yes	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP7	10:55	25.1	2.1	Ν	Yes	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP8	10:58	25.2	1.4	Ν	Yes	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP9	11:01	25.4	0.7	Ν	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP10	11:04	25.2	2.6	Ν	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP11	11:14	25.3	3.2	Е	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP1	14:37	24.8	1.3	S	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP2	14:40	23.1	3.1	S	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP3	14:43	25.1	1.1	SW	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP4	14:46	24.8	2.3	Е	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP5	14:49	24.0	2.2	S	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP6	14:52	24.6	3.1	S	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature	-		From	Odour	Odour Chanadariatia	Possible Source	Remarks
11.5		0.05		(oC)	(m/s)	Direction	Project Site		Characteristic	27/1	
14-Dec-21	Sunny	OP7	14:55	25.0	1.8	S	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP8	14:59	25.0	2.9	S	No	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP9	15:03	24.2	2.4	E	Yes	1	Acidic	Town gas	N/A
14-Dec-21	Sunny	OP10	15:08	24.6	1.3	SE	Yes	0	N/A	N/A	N/A
14-Dec-21	Sunny	OP11	15:20	24.7	1.4	Е	No	0	N/A	N/A	N/A
14-Dec-21	Fine	OP1	18:07	24.3	0.8	S	No	0	N/A	N/A	N/A
14-Dec-21	Fine	OP2	18:10	24.1	0.4	S	No	0	N/A	N/A	N/A
14-Dec-21	Fine	OP3	18:15	23.7	0.5	Е	No	0	N/A	N/A	N/A
14-Dec-21	Fine	OP4	18:19	23.4	0.9	Е	No	0	N/A	N/A	N/A
14-Dec-21	Fine	OP5	18:24	23.1	2.3	Е	No	0	N/A	N/A	N/A
14-Dec-21	Fine	OP6	18:29	23.2	0.6	NE	Yes	0	N/A	N/A	N/A
14-Dec-21	Fine	OP7	18:33	23.1	1.3	S	No	0	N/A	N/A	N/A
14-Dec-21	Fine	OP8	18:37	23.3	0.8	Ν	Yes	0	N/A	N/A	N/A
14-Dec-21	Fine	OP9	18:40	22.9	0.5	S	No	0	N/A	N/A	N/A
14-Dec-21	Fine	OP10	18:44	22.9	0.6	Ν	No	0	N/A	N/A	N/A
14-Dec-21	Fine	OP11	18:53	22.8	0.7	W	No	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP1	10:37	23.6	2.0	S	No	1	Grassy	Vegetation	N/A
15-Dec-21	Overcast	OP2	10:40	23.2	1.8	S	No	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP3	10:43	22.4	1.1	SW	No	1	Diesel	Generator	N/A
15-Dec-21	Overcast	OP4	10:46	22.1	2.5	Е	No	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP5	10:50	22.4	3.8	Е	No	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP6	10:55	22.2	3.4	SE	No	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP7	10:58	24.0	1.7	NW	Yes	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP8	11:01	23.2	1.8	NW	Yes	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP9	11:04	23.9	2.6	NW	Yes	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP10	11:07	23.5	1.2	NW	Yes	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP11	11:15	24.3	1.2	SW	Yes	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP1	14:33	23.2	0.4	N	Yes	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP2	14:36	23.8	0.5	S	No	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP3	14:39	23.4	0.6	N	Yes	1	Oil	Generator	N/A
15-Dec-21 15-Dec-21	Overcast	OP4	14:43	23.9	1.4	E	No	0	N/A	N/A	N/A
15-Dec-21 15-Dec-21	Overcast	OP5	14:45 14:47	23.3	2.4	E	No	0	N/A	N/A	N/A
15-Dec-21 15-Dec-21	Overcast	OP6	14.47	22.8	3.0	L N	Yes	0	N/A	N/A	N/A
15-Dec-21 15-Dec-21		OP6 OP7	14:51 14:55	22.8	3.0 2.5	N	Yes	0	N/A	N/A N/A	N/A N/A
15-Dec-21 15-Dec-21	Overcast	OP7 OP8	14:55 14:59	23.2 22.9		N NE					
	Overcast				2.4		Yes	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP9	15:02	23.5	2.3	N N	No	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP10	15:05	23.6	0.9	N	No	0	N/A	N/A	N/A
15-Dec-21	Overcast	OP11	15:13	23.3	1.1	SE	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
15-Dec-21	Fine	OP1	18:25	21.9	0.2	S	No	0	N/A	N/A	N/A
15-Dec-21	Fine	OP2	18:29	21.7	0.3	S	No	0	N/A	N/A	N/A
15-Dec-21	Fine	OP3	18:34	21.5	0.6	Е	No	0	N/A	N/A	N/A
15-Dec-21	Fine	OP4	18:38	21.6	1.8	Е	No	0	N/A	N/A	N/A
15-Dec-21	Fine	OP5	18:41	22.1	2.7	NE	Yes	0	N/A	N/A	N/A
15-Dec-21	Fine	OP6	18:43	22.3	1.4	Ν	Yes	0	N/A	N/A	N/A
15-Dec-21	Fine	OP7	18:45	21.7	0.8	Ν	Yes	0	N/A	N/A	N/A
15-Dec-21	Fine	OP8	18:48	22.2	2.2	Ν	Yes	0	N/A	N/A	N/A
15-Dec-21	Fine	OP9	18:52	23.0	1.3	Ν	No	0	N/A	N/A	N/A
15-Dec-21	Fine	OP10	18:55	22.8	0.6	Ν	No	0	N/A	N/A	N/A
15-Dec-21	Fine	OP11	19:04	21.4	0.6	Ν	No	0	N/A	N/A	N/A
16-Dec-21	Fine	OP1	10:35	25.8	1.2	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Fine	OP2	10:39	25.7	2.5	SW	Yes	0	N/A	N/A	N/A
16-Dec-21	Fine	OP3	10:43	25.9	0.6	Ν	Yes	1	Oil	Generator	N/A
16-Dec-21	Fine	OP4	10:47	25.4	3.2	Е	No	0	N/A	N/A	N/A
16-Dec-21	Fine	OP5	10:51	25.3	3.6	Е	No	0	N/A	N/A	N/A
16-Dec-21	Fine	OP6	10:54	25.4	1.1	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Fine	OP7	10:58	25.6	0.9	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Fine	OP8	11:01	25.5	2.4	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Fine	OP9	11:04	25.4	2.2	Ν	No	1	Acidic	Town gas	N/A
16-Dec-21	Fine	OP10	11:07	25.6	1.8	Ν	No	0	N/A	N/A	N/A
16-Dec-21	Fine	OP11	11:17	25.9	3.3	SE	No	0	N/A	N/A	N/A
16-Dec-21	Overcast	OP1	14:41	24.5	1.5	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Overcast	OP2	14:44	24.7	0.6	S	No	0	N/A	N/A	N/A
16-Dec-21	Overcast	OP3	14:47	24.2	1.3	Ν	Yes	1	Oil	Generator	N/A
16-Dec-21	Overcast	OP4	14:51	24.8	1.2	Е	No	0	N/A	N/A	N/A
16-Dec-21	Overcast	OP5	14:54	25.2	2.2	Е	No	0	N/A	N/A	N/A
16-Dec-21	Overcast	OP6	14:57	24.6	1.6	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Overcast	OP7	15:01	24.3	2.6	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Overcast	OP8	15:05	25.7	1.5	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Overcast	OP9	15:08	24.6	1.1	Ν	No	0	N/A	N/A	N/A
16-Dec-21	Overcast	OP10	15:11	25.6	1.0	Ν	No	0	N/A	N/A	N/A
16-Dec-21	Overcast	OP11	15:15	24.3	2.3	E	No	0	N/A	N/A	N/A
16-Dec-21	Fine	OP1	18:15	23.2	1.8	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Fine	OP2	18:19	23.4	1.2	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Fine	OP3	18:23	22.9	1.4	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Fine	OP4	18:26	23.1	1.8	Ν	Yes	0	N/A	N/A	N/A
16-Dec-21	Fine	OP5	18:30	23.3	1.2	Ν	Yes	0	N/A	N/A	N/A

16-Dec-21 16-Dec-21 16-Dec-21 16-Dec-21 16-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21	Fine Fine Fine Fine Fine Fine Fine	OP6 OP7 OP8 OP9 OP10 OP11	18:33 18:37 18:41 18:45 18:48	(oC) 22.9 22.8 22.9 23.0	(m/s) 1.1 1.3 1.9	Direction N N	Project Site Yes	0	Characteristic N/A		27/1
16-Dec-21 16-Dec-21 16-Dec-21 16-Dec-21 16-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21	Fine Fine Fine Fine Fine Fine Fine	OP7 OP8 OP9 OP10 OP11	18:37 18:41 18:45	22.8 22.9	1.3			0	ΝΙΙΔ		
16-Dec-21 16-Dec-21 16-Dec-21 16-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21	Fine Fine Fine Fine Fine Fine	OP8 OP9 OP10 OP11	18:41 18:45	22.9		IN	3/			N/A	N/A
16-Dec-21 16-Dec-21 16-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21	Fine Fine Fine Fine Fine	OP9 OP10 OP11	18:45		1.9		Yes	0	N/A	N/A	N/A
16-Dec-21 16-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21	Fine Fine Fine Fine	OP10 OP11		23.0		N	Yes	0	N/A	N/A	N/A
16-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21	Fine Fine Fine	OP11	18:48		1.6	N	No	0	N/A	N/A	N/A
17-Dec-21 17-Dec-21 17-Dec-21 17-Dec-21	Fine Fine			22.1	2.3	Ν	No	0	N/A	N/A	N/A
17-Dec-21 17-Dec-21 17-Dec-21	Fine		18:56	23.2	0.8	Ν	No	0	N/A	N/A	N/A
17-Dec-21 17-Dec-21		OP1	10:42	23.9	2.9	Ν	Yes	0	N/A	N/A	N/A
17-Dec-21		OP2	10:45	23.2	3.2	Ν	Yes	0	N/A	N/A	N/A
	Fine	OP3	10:48	23.3	1.7	Ν	Yes	1	Oil	Generator	N/A
	Fine	OP4	10:51	24.1	1.2	NE	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP5	10:54	23.5	0.6	Ν	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP6	10:57	23.2	4.1	Ν	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP7	11:00	23.1	3.7	Ν	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP8	11:04	23.2	4.2	Ν	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP9	11:06	22.9	3.5	Ν	No	0	N/A	N/A	N/A
17-Dec-21	Fine	OP10	11:08	23.5	0.7	Ν	No	0	N/A	N/A	N/A
17-Dec-21	Fine	OP11	11:21	24.2	0.7	Е	No	0	N/A	N/A	N/A
17-Dec-21	Fine	OP1	14:37	22.3	4.0	NW	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP2	14:39	21.9	5.3	NW	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP3	14:42	22.9	2.1	NE	No	1	Diesel	Generator	N/A
17-Dec-21	Fine	OP4	14:45	22.8	2.5	NE	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP5	14:48	22.4	3.8	NE	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP6	14:50	22.1	3.5	Ν	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP7	14:55	22.6	4.8	NW	No	1	Burnt	Welding	N/A
17-Dec-21	Fine	OP8	14:59	22.8	2.6	Ν	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP9	15:02	22.2	2.2	N	No	0	N/A	N/A	N/A
17-Dec-21	Fine	OP10	15:04	22.9	0.7	N	No	0	N/A	N/A	N/A
17-Dec-21	Fine	OP11	15:12	21.6	5.1	E	No	0	N/A	N/A	N/A
17-Dec-21	Fine	OP1	18:20	21.1	7.2	N	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP2	18:23	21.4	1.8	N	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP3	18:27	21.3	3.1	N	Yes	0	N/A	N/A	N/A
17-Dec-21	Fine	OP4	18:30	21.3	0.8	NE	Yes	1	Acidic	Leachate Treatment Plant	
17-Dec-21 17-Dec-21	Fine	OP5	18:33	21.4	3.2	E	No	0	N/A	N/A	N/A
17-Dec-21 17-Dec-21	Fine	OP6	18:35	21.2	4.2	N	Yes	0	N/A	N/A N/A	N/A
17-Dec-21 17-Dec-21	Fine	OP7	18:37	21.1 21.3	4.2 3.4	N	Yes	0	N/A	N/A	N/A
17-Dec-21 17-Dec-21	Fine	OP7 OP8	18:41 18:44	21.5 21.0	3.4 4.3	N N	Yes	0	N/A N/A	N/A N/A	N/A N/A
17-Dec-21 17-Dec-21	Fine	OP8 OP9	18:44 18:47	21.0 21.9		N	No		N/A N/A	N/A	N/A N/A
	Fine	OP9 OP10	18:47 18:51	21.9 22.0	2.2 1.9	N NW	No No	0 0	N/A N/A	N/A N/A	N/A N/A

Date	Weather	Location	Time	Temperature	-		From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
17 0 01	<b>T</b> .	0011	10.07	(oC)	(m/s)	Direction	Project Site			NT / A	NT / A
17-Dec-21	Fine	OP11	19:07	21.2	3.8	SE	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP1	10:50	19.1	4.3	N	Yes	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP2	10:54	20.2	3.0	N	Yes	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP3	10:59	22.0	2.2	SW	No	1	Oil	Generator	N/A
18-Dec-21	Sunny	OP4	11:03	23.6	1.2	E	No	1	Leachate	Leachate Treatment Plant	
18-Dec-21	Sunny	OP5	11:07	21.2	4.1	NW	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP6	11:11	19.3	2.7	N	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP7	11:15	19.2	2.4	Ν	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP8	11:19	19.3	1.8	NW	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP9	11:23	19.4	2.5	NW	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP10	11:27	21.2	1.6	NW	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP11	11:40	20.8	2.1	Е	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP1	14:40	21.9	2.1	Ν	Yes	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP2	14:44	22.2	1.3	NW	Yes	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP3	14:48	25.9	1.7	NE	No	1	Oil	Generator	N/A
18-Dec-21	Sunny	OP4	14:52	26.7	0.8	NE	Yes	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP5	14:55	25.5	1.9	NW	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP6	14:59	23.1	2.7	Ν	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP7	15:03	22.7	3.9	Ν	Yes	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP8	15:06	21.4	3.0	Ν	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP9	15:10	22.8	1.8	NE	Yes	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP10	15:13	22.1	2.7	NW	No	0	N/A	N/A	N/A
18-Dec-21	Sunny	OP11	15:23	23.3	1.4	Е	No	0	N/A	N/A	N/A
18-Dec-21	Fine	OP1	18:06	18.8	1.7	Ν	Yes	0	N/A	N/A	N/A
18-Dec-21	Fine	OP2	18:09	18.9	2.5	Ν	Yes	0	N/A	N/A	N/A
18-Dec-21	Fine	OP3	18:13	19.1	1.4	NW	Yes	0	N/A	N/A	N/A
18-Dec-21	Fine	OP4	18:17	19.0	2.1	NE	Yes	0	N/A	N/A	N/A
18-Dec-21	Fine	OP5	18:20	19.4	0.7	NE	Yes	0	N/A	N/A	N/A
18-Dec-21	Fine	OP6	18:24	19.7	2.1	Ν	Yes	0	N/A	N/A	N/A
18-Dec-21	Fine	OP7	18:28	19.3	2.3	Ν	No	0	N/A	N/A	Ń/A
18-Dec-21	Fine	OP8	18:32	19.1	2.2	NW	No	0	N/A	N/A	N/A
18-Dec-21	Fine	OP9	18:36	19.3	1.2	NW	No	0	N/A	N/A	N/A
18-Dec-21	Fine	OP10	18:39	19.6	0.5	NE	Yes	0	N/A	N/A	N/A
18-Dec-21	Fine	OP11	18:48	19.2	1.5	SE	No	0	N/A	N/A	N/A
10 Dec 21 19-Dec-21	Sunny	OP1	10:10	19.6	1.6	NW	Yes	0	N/A	N/A	N/A
19-Dec-21 19-Dec-21	Sunny	OP2	10:34	20.1	0.1	S	No	0	N/A	N/A	N/A
19-Dec-21	Sunny	OP3	10:30	21.0	0.6	E	No	0	N/A	N/A	N/A
19-Dec-21 19-Dec-21	Sunny	OP4	10:42	21.3	1.2	E	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
19-Dec-21	Sunny	OP5	10:48	21.7	1.3	NW	No	0	N/A	N/A	N/A
19-Dec-21	Sunny	OP6	10:52	21.4	1.5	N	Yes	0	N/A	N/A	N/A
19-Dec-21	Sunny	OP7	10:55	20.5	3.1	Ν	Yes	0	N/A	Ň/A	N/A
19-Dec-21	Sunny	OP8	10:59	20.1	1.8	Ν	Yes	0	N/A	N/A	N/A
19-Dec-21	Sunny	OP9	11:04	21.1	2.6	NW	No	0	N/A	N/A	N/A
19-Dec-21	Sunny	OP10	11:07	21.9	1.1	NW	No	0	N/A	N/A	N/A
19-Dec-21	Sunny	OP11	11:13	21.9	2.3	Е	No	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP1	15:52	20.7	0.9	S	No	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP2	15:47	20.6	1.4	S	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP3	15:43	20.6	1.6	NE	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP4	15:39	20.9	2.1	Е	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP5	15:34	22.4	1.8	SE	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP6	15:29	22.1	1.1	SE	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP7	15:24	20.9	4.3	Ν	No	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP8	15:20	21.1	3.8	Ν	No	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP9	15:15	20.7	0.8	NE	No	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP10	15:11	21.0	1.8	Е	No	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP11	15:06	23.1	1.0	Ν	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP1	18:06	19.6	1.3	Ν	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP2	18:10	19.8	0.4	SE	No	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP3	18:13	19.8	0.5	NE	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP4	18:17	20.0	0.8	Е	No	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP5	18:21	19.7	1.7	Е	No	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP6	18:24	19.6	1.4	Ν	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP7	18:28	19.8	1.5	Ν	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP8	18:32	19.5	1.2	Ν	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP9	18:36	19.9	1.2	NE	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP10	18:40	19.8	1.3	NE	Yes	0	N/A	N/A	N/A
19-Dec-21	Overcast	OP11	18:49	19.9	0.5	SE	Yes	0	N/A	N/A	N/A
20-Dec-21	Shower	OP1	10:37	14.9	2.0	NW	Yes	0	N/A	N/A	N/A
20-Dec-21	Shower	OP2	10:38	14.9	1.0	NW	Yes	0	N/A	N/A	N/A
20-Dec-21	Shower	OP3	10:41	14.8	0.6	NE	No	1	Diesel	Generator	N/A
20-Dec-21	Shower	OP4	10:44	14.8	1.7	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Shower	OP5	10:46	15.5	1.8	Е	No	0	N/A	N/A	N/A
20-Dec-21	Shower	OP6	10:48	15.2	2.4	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Shower	OP7	10:50	15.0	3.8	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Shower	OP8	10:52	14.6	3.6	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Shower	OP9	10:54	14.7	1.6	Ν	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
20-Dec-21	Shower	OP10	10:56	14.5	3.2	NE	No	0	N/A	N/A	N/A
20-Dec-21	Shower	OP11	11:03	15.2	1.3	Е	No	0	N/A	N/A	N/A
20-Dec-21	Overcast	OP1	14:33	15.3	2.0	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Overcast	OP2	14:37	15.6	0.8	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Overcast	OP3	14:40	16.2	0.4	NE	Yes	1	Oil	Generator	N/A
20-Dec-21	Overcast	OP4	14:43	15.9	1.4	Е	No	0	N/A	N/A	N/A
20-Dec-21	Overcast	OP5	14:46	14.8	1.2	Е	No	0	N/A	N/A	N/A
20-Dec-21	Overcast	OP6	14:48	15.1	2.1	NE	Yes	0	N/A	N/A	N/A
20-Dec-21	Overcast	OP7	14:51	16.2	1.5	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Overcast	OP8	14:53	15.7	1.8	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Overcast	OP9	14:56	16.2	1.2	Ν	No	0	N/A	N/A	N/A
20-Dec-21	Overcast	OP10	14:58	15.8	0.7	Ν	No	0	N/A	N/A	N/A
20-Dec-21	Overcast	OP11	15:07	16.1	1.0	Е	No	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP1	18:05	15.6	1.3	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP2	18:09	15.8	0.2	S	No	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP3	18:12	15.1	0.5	S	No	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP4	18:16	15.3	0.8	Е	No	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP5	18:20	15.7	0.5	Е	No	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP6	18:23	15.1	1.2	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP7	18:26	15.3	1.6	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP8	18:30	15.6	1.2	Ν	Yes	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP9	18:33	16.0	0.4	Ν	No	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP10	18:37	15.7	0.5	Ν	No	0	N/A	N/A	N/A
20-Dec-21	Rainy	OP11	18:47	15.3	0.6	Ν	No	0	N/A	N/A	N/A
21-Dec-21	Shower	OP1	10:34	17.1	3.3	Ν	Yes	0	N/A	N/A	N/A
21-Dec-21	Shower	OP2	10:38	17.4	4.2	Ν	Yes	0	N/A	N/A	N/A
21-Dec-21	Shower	OP3	10:42	17.1	1.8	Ν	Yes	1	Oil	Generator	N/A
21-Dec-21	Shower	OP4	10:44	17.2	1.4	Ν	Yes	1	Acidic	Leachate Treatment Plant	N/A
21-Dec-21	Shower	OP5	10:47	17.0	1.8	NW	No	0	N/A	N/A	N/A
21-Dec-21	Shower	OP6	10:50	16.8	3.5	Ν	Yes	0	N/A	N/A	N/A
21-Dec-21	Shower	OP7	10:53	16.5	3.3	Ν	Yes	0	N/A	N/A	N/A
21-Dec-21	Shower	OP8	10:55	16.8	2.3	Ν	Yes	1	Oil	Generator	N/A
21-Dec-21	Shower	OP9	10:57	17.9	0.9	Ν	No	0	N/A	N/A	N/A
21-Dec-21	Shower	OP10	11:00	17.1	1.8	Ν	No	0	N/A	N/A	N/A
21-Dec-21	Shower	OP11	11:09	17.5	1.5	Е	No	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP1	14:58	19.7	0.9	NW	Yes	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP2	15:03	18.7	1.0	Ν	Yes	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP3	15:07	19.9	0.5	Ν	Yes	1	Oil	Generator	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
21-Dec-21	Overcast	OP4	15:11	20.0	1.1	E	No	1	Acidic Gas	Leachate Treatment Plant	N/A
21-Dec-21	Overcast	OP5	15:15	18.8	1.8	NW	No	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP6	15:19	18.6	1.8	Ν	Yes	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP7	15:22	18.1	1.7	Ν	Yes	0	N/A	N/A	, N/A
21-Dec-21	Overcast	OP8	15:25	18.8	0.8	Ν	Yes	0	N/A	N/A	, N/A
21-Dec-21	Overcast	OP9	15:30	18.4	2.6	NW	No	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP10	15:33	18.3	0.7	NW	No	0	N/A	N/A	Ň/A
21-Dec-21	Overcast	OP11	15:43	18.4	1.1	Е	No	0	N/A	N/A	, N/A
21-Dec-21	Overcast	OP1	18:45	17.5	0.8	Ν	Yes	0	N/A	N/A	, N/A
21-Dec-21	Overcast	OP2	18:48	17.4	0.9	Ν	Yes	0	, N/A	N/A	N/A
21-Dec-21	Overcast	OP3	18:50	17.0	1.2	Ν	Yes	0	N/A	N/A	, N/A
21-Dec-21	Overcast	OP4	18:52	17.2	0.7	Е	No	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP5	18:55	16.9	0.7	Е	No	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP6	18:59	17.0	2.9	Ν	Yes	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP7	19:02	17.9	2.5	Ν	Yes	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP8	19:05	17.5	1.2	N	Yes	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP9	19:09	17.8	0.3	Ν	No	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP10	19:13	18.0	1.4	NE	Yes	0	N/A	N/A	N/A
21-Dec-21	Overcast	OP11	19:23	18.1	3.4	Е	No	0	N/A	N/A	Ń/A
22-Dec-21	Overcast	OP1	10:38	19.3	2.4	Ν	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP2	10:41	19.7	2.8	Ν	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP3	10:45	19.8	1.5	NE	No	1	Oil	Generator	N/A
22-Dec-21	Overcast	OP4	10:48	19.7	1.2	Ν	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP5	10:52	19.8	1.9	Ν	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP6	10:54	20.4	2.8	Ν	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP7	10:57	20.5	2.4	Ν	Yes	0	N/A	N/A	Ń/A
22-Dec-21	Overcast	OP8	11:00	20.5	2.3	Ν	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP9	11:04	20.8	2.4	Ν	No	0	N/A	N/A	Ń/A
22-Dec-21	Overcast	OP10	11:09	20.9	1.4	Ν	No	0	N/A	N/A	Ń/A
22-Dec-21	Overcast	OP11	11:22	22.3	2.1	SW	Yes	0	N/A	N/A	Ń/A
22-Dec-21	Overcast	OP1	14:30	22.6	1.0	Ν	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP2	14:33	22.2	1.3	NW	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP3	14:36	23.6	0.5	Ν	Yes	0	N/A	N/A	Ň/A
22-Dec-21	Overcast	OP4	14:38	23.4	1.4	Е	No	0	N/A	N/A	Ň/A
22-Dec-21	Overcast	OP5	14:41	22.3	1.0	Е	No	0	N/A	N/A	, N/A
22-Dec-21	Overcast	OP6	14:43	22.3	0.9	S	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP7	14:46	22.7	0.9	Ν	Yes	0	N/A	N/A	Ń/A
22-Dec-21	Overcast	OP8	14:49	22.7	0.8	N	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
22-Dec-21	Overcast	OP9	14:51	22.5	1.5	SE	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP10	14:54	22.6	0.9	NE	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP11	15:04	21.4	1.5	SE	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP1	18:20	18.5	1.1	N	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP2	18:24	18.5	0.7	N	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP3	18:28	18.1	2.1	W	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP4	18:31	18.9	0.4	W	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP5	18:34	18.7	1.3	Е	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP6	18:37	18.3	2.4	Ν	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP7	18:40	18.6	1.7	Ν	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP8	18:44	18.5	1.4	NE	Yes	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP9	18:48	18.6	0.5	N	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP10	18:51	18.7	0.5	N	No	0	N/A	N/A	N/A
22-Dec-21	Overcast	OP11	19:10	18.4	1.2	NE	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP1	10:30	22.1	3.3	Ν	Yes	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP2	10:33	22.5	0.7	S	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP3	10:37	22.3	1.4	Ν	Yes	1	Oil	Electric Generator	N/A
23-Dec-21	Overcast	OP4	10:41	22.6	2.8	Е	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP5	10:45	22.4	3.6	Е	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP6	10:48	22.3	3.4	Ν	Yes	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP7	10:51	22.2	2.1	Ν	Yes	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP8	10:54	22.3	2.8	Ν	Yes	1	Oil	Electric Generator	N/A
23-Dec-21	Overcast	OP9	10:59	22.6	1.2	Ν	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP10	11:03	22.5	1.5	Ν	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP11	11:14	22.8	1.9	W	Yes	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP1	14:40	23.3	1.6	Ν	Yes	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP2	14:45	22.8	1.4	S	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP3	14:48	21.4	0.5	Ν	Yes	1	Oil	Electric Generator	N/A
23-Dec-21	Overcast	OP4	14:51	20.8	2.3	Е	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP5	14:54	21.2	1.3	Е	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP6	14:57	21.0	2.2	S	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP7	15:01	21.2	1.2	Ν	Yes	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP8	15:04	21.0	0.8	Ν	Yes	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP9	15:07	21.4	1.3	SE	Yes	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP10	15:11	21.5	0.4	Ν	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP11	15:23	21.9	0.7	NE	No	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP1	18:05	18.5	0.5	Ν	Yes	0	N/A	N/A	N/A
23-Dec-21	Overcast	OP2	18:09	18.1	0.4	Ν	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intonsity	Odour Characteristic	Possible Source	Remarks
23-Dec-21	Overcast	OP3	18:13	17.6	0.4	N	Yes	0	N/A	N/A	N/A
23-Dec-21 23-Dec-21	Overcast Overcast	OP3 OP4	18:13	17.8	0.4 0.6	E	No	0	N/A	N/A N/A	N/A N/A
23-Dec-21 23-Dec-21	Overcast	OP5	18:20	18.0	0.7	E	No	0	N/A	N/A N/A	N/A
23-Dec-21 23-Dec-21	Overcast	OP6	18:20 18:24	18.1	0.7	E	Yes	0	N/A	N/A N/A	N/A
23-Dec-21 23-Dec-21	Overcast	OP7	18.24 18:27	18.2	0.7	L N	Yes	0	N/A	N/A N/A	N/A N/A
23-Dec-21 23-Dec-21	Overcast	OP8	18:27	18.2	0.0	N	Yes	0	N/A	N/A N/A	N/A N/A
23-Dec-21 23-Dec-21	Overcast	OP9	18.31 18:35	18.0	0.4	N	No	0	N/A	N/A N/A	N/A N/A
23-Dec-21 23-Dec-21	Overcast	OP10	18.35 18:40	17.8	0.5	N	No	0	N/A	N/A N/A	N/A
23-Dec-21 23-Dec-21	Overcast	OP10 OP11	18:52	17.8	0.5	NE	No	0	N/A	N/A N/A	N/A N/A
23-Dec-21 24-Dec-21		OP11 OP1	10:52	20.3	0.3	N	Yes	0	N/A	N/A N/A	N/A N/A
24-Dec-21 24-Dec-21	Overcast Overcast	OP1 OP2	10:40	20.3	0.4		N/A	0		N/A N/A	
		OP2 OP3				N/A			N/A		N/A
24-Dec-21	Overcast		10:47	19.9	0.6	N	Yes	1	Oil	Electric Generator	N/A
24-Dec-21	Overcast	OP4 OP5	10:50 10:54	20.1 20.0	0.7	N	Yes No	0	N/A	N/A	N/A
24-Dec-21	Overcast				0.9	E		0	N/A	N/A	N/A
24-Dec-21	Overcast	OP6	10:58	20.1	0.4	S	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP7	11:02	19.7	0.6	N	Yes	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP8	11:05	19.9	0.8	N	Yes	1	Oil	Electric Generator	N/A
24-Dec-21	Overcast	OP9	11:08	20.4	0.0	N/A	N/A	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP10	11:12	21.0	0.9	N	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP11	11:22	20.5	1.3	E	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP1	14:38	22.0	0.0	N/A	N/A	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP2	14:41	21.6	1.2	S	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP3	14:43	22.3	0.7	SW	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP4	14:45	23.7	0.0	N/A	N/A	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP5	14:47	23.1	0.5	SW	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP6	14:49	22.3	1.3	S	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP7	14:52	22.1	2.2	S	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP8	14:55	22.9	0.9	S	No	1	Diesel	Generator	N/A
24-Dec-21	Overcast	OP9	14:58	22.1	1.3	S	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP10	14:59	22.1	1.9	S	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP11	15:07	22.2	0.0	N/A	N/A	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP1	18:00	19.0	0.4	Ν	Yes	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP2	18:03	19.1	0.0	N/A	N/A	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP3	18:07	19.4	0.0	N/A	N/A	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP4	18:10	18.8	0.4	Ν	Yes	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP5	18:14	18.7	0.2	Ν	Yes	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP6	18:17	18.8	0.3	Ν	Yes	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP7	18:21	18.5	0.7	Ν	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
24-Dec-21	Overcast	OP8	18:25	18.6	0.4	Ν	Yes	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP9	18:29	18.3	0.4	Ν	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP10	18:33	18.1	0.5	Ν	No	0	N/A	N/A	N/A
24-Dec-21	Overcast	OP11	18:44	17.6	0.6	Е	No	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP1	11:00	20.5	1.3	S	No	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP2	11:03	20.7	2.3	S	No	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP3	11:07	20.2	2.9	W	No	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP4	11:10	21.1	3.9	Е	No	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP5	11:14	21.3	3.5	Е	No	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP6	11:17	21.1	4.1	Е	Yes	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP7	11:20	22.7	1.4	S	No	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP8	11:23	22.9	1.4	S	No	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP9	11:25	22.8	1.2	Ν	No	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP10	11:28	22.3	1.6	NE	Yes	0	N/A	N/A	N/A
25-Dec-21	Sunny	OP11	11:40	23.3	0.6	Ν	No	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP1	14:50	22.1	1.3	S	No	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP2	14:53	21.4	0.6	Ν	Yes	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP3	14:57	20.3	1.4	SW	No	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP4	15:00	20.0	1.3	Е	No	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP5	15:04	19.8	3.2	Е	No	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP6	15:08	19.7	1.8	Ν	Yes	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP7	15:12	20.6	1.4	S	No	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP8	15:16	20.8	1.5	Ν	Yes	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP9	15:20	20.1	1.4	Ν	No	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP10	15:23	20.2	0.6	Ν	No	0	N/A	N/A	N/A
25-Dec-21	Overcast	OP11	15:35	19.5	0.9	S	Yes	0	N/A	N/A	N/A
25-Dec-21	Fine	OP1	18:00	19.5	0.6	Ν	Yes	0	N/A	N/A	N/A
25-Dec-21	Fine	OP2	18:03	18.8	0.7	S	No	0	N/A	N/A	N/A
25-Dec-21	Fine	OP3	18:07	18.2	0.4	Ν	Yes	0	N/A	N/A	N/A
25-Dec-21	Fine	OP4	18:10	18.1	0.5	Е	No	0	N/A	N/A	N/A
25-Dec-21	Fine	OP5	18:13	18.0	0.6	Е	No	0	N/A	N/A	N/A
25-Dec-21	Fine	OP6	18:15	17.8	1.0	S	No	0	N/A	N/A	N/A
25-Dec-21	Fine	OP7	18:18	17.5	0.9	Ν	Yes	0	N/A	N/A	N/A
25-Dec-21	Fine	OP8	18:21	17.5	0.6	Ν	Yes	0	N/A	N/A	N/A
25-Dec-21	Fine	OP9	18:25	17.4	1.8	Е	Yes	0	N/A	N/A	N/A
25-Dec-21	Fine	OP10	18:29	17.5	1.9	Ν	No	0	N/A	N/A	N/A
25-Dec-21	Fine	OP11	18:41	17.2	2.9	NE	No	0	N/A	N/A	N/A
26-Dec-21	Overcast	OP1	10:40	15.7	1.7	Ν	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
26-Dec-21	Overcast	OP2	10:43	16.6	1.3	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Overcast	OP3	10:47	16.5	1.2	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Overcast	OP4	10:51	16.7	1.4	Е	No	0	N/A	N/A	N/A
26-Dec-21	Overcast	OP5	10:54	15.6	2.3	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Overcast	OP6	10:58	16.0	1.7	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Overcast	OP7	11:02	16.1	2.7	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Overcast	OP8	11:06	15.7	3.7	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Overcast	OP9	11:10	15.2	2.0	Ν	No	0	N/A	N/A	N/A
26-Dec-21	Overcast	OP10	11:13	15.8	3.1	Ν	No	0	N/A	N/A	N/A
26-Dec-21	Overcast	OP11	11:21	15.6	0.7	Е	No	0	N/A	N/A	N/A
26-Dec-21	Shower	OP1	15:22	14.4	1.7	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP2	15:19	14.3	3.3	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP3	15:15	14.8	2.3	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP4	15:12	15.4	0.6	Е	No	1	Acidic	Leachate Treatment Plant	N/A
26-Dec-21	Shower	OP5	15:07	14.9	1.9	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP6	15:03	15.1	1.4	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP7	14:59	14.8	2.6	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP8	14:55	14.9	3.3	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP9	14:51	15.2	2.3	Ν	No	0	N/A	N/A	N/A
26-Dec-21	Shower	OP10	14:47	15.7	2.1	Ν	No	0	N/A	N/A	N/A
26-Dec-21	Shower	OP11	14:39	15.4	1.1	Е	No	0	N/A	N/A	N/A
26-Dec-21	Shower	OP1	18:02	13.2	2.8	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP2	18:06	13.3	4.2	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP3	18:11	13.2	1.4	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP4	18:14	13.1	2.4	NE	No	1	Acidic	Leachate Treatment Plant	N/A
26-Dec-21	Shower	OP5	18:17	13.0	3.3	Е	No	0	N/A	N/A	N/A
26-Dec-21	Shower	OP6	18:21	12.9	4.3	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP7	18:25	12.5	5.1	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP8	18:29	12.4	6.3	Ν	Yes	0	N/A	N/A	N/A
26-Dec-21	Shower	OP9	18:33	12.3	2.7	Ν	No	0	N/A	N/A	N/A
26-Dec-21	Shower	OP10	18:37	12.4	3.5	Ν	No	0	N/A	N/A	N/A
26-Dec-21	Shower	OP11	18:46	12.2	1.1	Е	No	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP1	10:50	13.0	2.2	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP2	10:53	14.0	1.2	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP3	10:56	14.1	1.7	NE	No	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP4	10:59	14.3	1.1	W	No	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP5	11:03	14.8	2.2	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP6	11:07	14.6	3.0	Ν	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature	Wind Speed		From	Odour	Odour	Possible Source	Remarks
07 D 01	0	0.07	11 10	(oC)	(m/s)	Direction	Project Site	5	Characteristic		NT / A
27-Dec-21	Overcast	OP7	11:10	13.3	2.7	N	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP8	11:14	12.8	4.9	N	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP9	11:17	13.7	1.7	N	No	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP10	11:21	13.8	3.2	N	No	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP11	11:34	14.4	0.8	SW	Yes	0	N/A	N/A	N/A
27-Dec-21	Fine	OP1	14:38	13.8	3.5	N	Yes	0	N/A	N/A	N/A
27-Dec-21	Fine	OP2	14:41	14.1	2.6	N	Yes	0	N/A	N/A	N/A
27-Dec-21	Fine	OP3	14:45	14.6	1.5	NE	No	0	N/A	N/A	N/A
27-Dec-21	Fine	OP4	14:48	14.8	1.7	Ε	No	0	N/A	N/A	N/A
27-Dec-21	Fine	OP5	14:52	14.4	1.9	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Fine	OP6	14:55	14.5	2.4	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Fine	OP7	14:59	14.1	2.6	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Fine	OP8	15:02	14.4	2.0	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Fine	OP9	15:06	14.6	1.3	Ν	No	0	N/A	N/A	N/A
27-Dec-21	Fine	OP10	15:09	14.8	1.3	Ν	No	0	N/A	N/A	N/A
27-Dec-21	Fine	OP11	15:20	14.7	1.4	SW	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP1	18:05	12.2	1.8	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP2	18:08	12.3	1.7	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP3	18:11	12.1	2.3	NE	No	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP4	18:15	12.3	1.5	Е	No	1	Leachate	Leachate Treatment Plant	N/A
27-Dec-21	Overcast	OP5	18:18	12.2	1.3	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP6	18:22	11.9	2.8	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP7	18:25	11.7	3.7	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP8	18:29	11.6	3.5	Ν	Yes	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP9	18:33	11.8	2.5	Ν	No	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP10	18:36	11.9	2.6	Ν	No	0	N/A	N/A	N/A
27-Dec-21	Overcast	OP11	18:48	11.4	2.3	Е	No	0	N/A	N/A	N/A
28-Dec-21	Fine	OP1	10:30	16.5	2.8	Ν	Yes	0	N/A	N/A	N/A
28-Dec-21	Fine	OP2	10:33	16.7	1.6	N	Yes	0	N/A	N/A	N/A
28-Dec-21	Fine	OP3	10:36	16.8	2.3	E	No	1	Oil	Electric Generator	N/A
28-Dec-21	Fine	OP4	10:40	16.5	1.8	E	No	0	N/A	N/A	N/A
28-Dec-21	Fine	OP5	10:43	16.7	2.2	N	No	0	N/A	N/A	N/A
28-Dec-21	Fine	OP6	10:43	16.6	2.4	N	No	0	N/A	N/A	N/A
28-Dec-21	Fine	OP7	10:47	16.4	2.4	N	Yes	0	N/A	N/A	N/A
28-Dec-21 28-Dec-21	Fine	OP8	10:55	16.5	3.1	N	Yes	0	N/A	N/A	N/A
28-Dec-21 28-Dec-21	Fine	OP9	10:55	16.7	3.1 1.3	N	No	0	N/A	N/A	N/A N/A
28-Dec-21 28-Dec-21	Fine	OP10	10.39	16.4	2.5	N	No	0	N/A	N/A	N/A
28-Dec-21 28-Dec-21	Fine	OP10 OP11	11:03	16.4 16.8	2.5 1.7	n E	No	0		-	
20-Dec-21	rine	OFII	11:13	10.0	1./	E	100	U	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
28-Dec-21	Overcast	OP1	14:43	19.9	1.3	S	No	0	N/A	N/A	N/A
28-Dec-21 28-Dec-21	Overcast	OP2	14:43	19.9	2.7	S	No	0 1	Diesel	Vehicle	N/A
28-Dec-21	Overcast	OP3	14:51	19.3	0.4	SW	No	0	N/A	N/A	N/A
28-Dec-21	Overcast	OP4	14:54	19.2	0.4	W	No	0	N/A	N/A	N/A
28-Dec-21	Overcast	OP5	14:57	19.2	1.4	SE	No	0	N/A	N/A	N/A
28-Dec-21 28-Dec-21	Overcast	OP6	15:00	18.3	2.5	S	No	0 1	Diesel	Vehicle	N/A
28-Dec-21 28-Dec-21	Overcast	OP7	15:00 15:03	19.8	2.5	S	No	0	N/A	N/A	N/A N/A
28-Dec-21	Overcast	OP8	15:05 15:06	21.3	0.9	SW	No	1	Sludge	Vehicle	N/A
28-Dec-21 28-Dec-21	Overcast	OP9	15:10	20.2	0.9	S	No	1	Town gas	Town gas plant	N/A
28-Dec-21 28-Dec-21	Overcast	OP10	15:10	19.7	0.9	S	No	0	N/A	N/A	N/A
28-Dec-21 28-Dec-21	Overcast	OP11 OP11	15:12 15:21	19.3	1.1	SE	No	0	N/A	N/A	N/A
28-Dec-21 28-Dec-21	Overcast	OP1	13.21	19.3	1.1	N	Yes	0	N/A	N/A	N/A N/A
28-Dec-21 28-Dec-21	Overcast	OP2	18:10	15.9	0.5	N	Yes	0	N/A	N/A	N/A N/A
28-Dec-21 28-Dec-21	Overcast	OP2 OP3	18:13	15.4	0.8	NE	No	0	N/A	N/A N/A	N/A
28-Dec-21 28-Dec-21	Overcast	OP4	18:21	15.5	0.8	E	No	0	N/A	N/A N/A	N/A
28-Dec-21 28-Dec-21	Overcast	OP5	18:25	15.6	1.2	E	No	0	N/A	N/A	N/A
28-Dec-21 28-Dec-21	Overcast	OP6	18:29	15.5	1.2	L N	No	0	N/A	N/A	N/A
28-Dec-21 28-Dec-21	Overcast	OP7	18:33	15.4	0.8	N	Yes	0	N/A	N/A N/A	N/A
28-Dec-21 28-Dec-21	Overcast	OP7 OP8	18:35	15.2	0.8 1.3	N	Yes	0	N/A	N/A N/A	N/A N/A
28-Dec-21 28-Dec-21		OP9	18:41	15.2	1.5	N	No	0	N/A	N/A	N/A
28-Dec-21 28-Dec-21	Overcast	OP9 OP10	18:41 18:45	15.2 15.4		N N	No				•
	Overcast				1.0			0	N/A	N/A	N/A
28-Dec-21	Overcast	OP11 OP1	18:44	14.8	1.2	NE	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP1	10:37	23.4	0.4	NE	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP2	10:40	21.4	2.3	S	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP3	10:42	21.1	1.3	SW	No	1	Diesel	Generator	N/A
29-Dec-21	Fine	OP4	10:45	21.3	0.8	E	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP5	10:49	21.7	0.5	W	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP6	10:52	22.8	1.2	SE	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP7	10:55	22.3	0.8	NE	Yes	0	N/A	N/A	N/A
29-Dec-21	Fine	OP8	10:58	21.9	1.7	N	Yes	0	N/A	N/A	N/A
29-Dec-21	Fine	OP9	11:01	22.2	1.3	N	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP10	11:04	23.4	0.4	N	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP11	11:12	21.8	2.4	SE	No	1	Soil/Sand	Ground	N/A
29-Dec-21	Sunny	OP1	14:31	23.1	2.1	S	No	0	N/A	N/A	N/A
29-Dec-21	Sunny	OP2	14:34	23.7	2.6	S	No	1	Oil	Vehicle	N/A
29-Dec-21	Sunny	OP3	14:37	24.1	1.6	N	Yes	0	N/A	N/A	N/A
29-Dec-21	Sunny	OP4	14:40	24.5	0.9	N	Yes	0	N/A	N/A	N/A
29-Dec-21	Sunny	OP5	14:44	23.5	0.8	W	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature	Wind Speed	Wind Direction	From Project Site	Odour Intonsity	Odour Characteristic	Possible Source	Remarks
20 Dec 21	Courses	OP6	14:48	(oC)	(m/s)	S	No	5		Sewer	NT / A
29-Dec-21 29-Dec-21	Sunny Sunny	OP6 OP7	14:48 14:52	23.0 24.2	1.3 1.5	S S	No	1 0	Sludge N/A	N/A	N/A N/A
29-Dec-21 29-Dec-21	5	OP7 OP8	14:52 14:55	24.2 24.6	1.5 1.6	S S	No	0	N/A	N/A N/A	N/A N/A
29-Dec-21 29-Dec-21	Sunny	OP8 OP9	14:55 14:59	24.6 24.5	2.7	S S	No		N/A	N/A N/A	N/A N/A
29-Dec-21 29-Dec-21	Sunny	OP9 OP10	14:59 15:03	24.5 25.4	2.7 1.4	S S	No	0 0	N/A	N/A N/A	N/A N/A
	Sunny	OP10 OP11				S SW				-	
29-Dec-21 29-Dec-21	Sunny Fine	OP11 OP1	15:15 18:00	24.6 18.6	1.2 0.6	SW N	Yes Yes	0 0	N/A	N/A	N/A
				18.8		N			N/A	N/A	N/A
29-Dec-21	Fine	OP2 OP3	18:03 18:07	18.5 17.9	0.4	n NE	Yes	0	N/A	N/A	N/A
29-Dec-21	Fine				0.5		No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP4	18:10	18.1	0.5	E	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP5	18:14	18.2	2.1	N	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP6	18:17	18.3	1.4	N	No	1	Diesel	Vehicle	N/A
29-Dec-21	Fine	OP7	18:21	17.9	1.7	N	Yes	1	Diesel	Vehicle	N/A
29-Dec-21	Fine	OP8	18:25	17.8	1.0	N	Yes	0	N/A	N/A	N/A
29-Dec-21	Fine	OP9	18:29	17.9	0.4	N	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP10	18:34	17.6	0.9	N	No	0	N/A	N/A	N/A
29-Dec-21	Fine	OP11	18:45	15.9	0.8	NE	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP1	10:35	18.5	3.1	N	Yes	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP2	10:39	18.7	0.8	Ν	Yes	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP3	10:42	18.6	0.4	S	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP4	10:45	18.4	2.1	E	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP5	10:48	18.5	3.8	E	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP6	10:52	18.8	1.2	Ν	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP7	10:55	19.0	1.2	Ν	Yes	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP8	10:59	19.1	1.6	Ν	Yes	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP9	11:03	19.0	1.4	Ν	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP10	11:06	19.2	0.6	Ν	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP11	11:16	19.4	1.6	E	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP1	14:35	21.1	1.4	W	Yes	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP2	14:39	22.7	1.3	S	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP3	14:43	22.2	0.9	SE	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP4	14:47	21.4	1.2	E	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP5	14:51	21.3	2.3	E	No	1	Oil	Excavator	N/A
30-Dec-21	Sunny	OP6	14:55	21.0	2.2	E	Yes	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP7	14:59	21.1	1.6	S	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP8	15:03	21.4	3.3	S	No	0	N/A	N/A	N/A
30-Dec-21	Sunny	OP9	15:08	21.3	1.1	Е	Yes	1	Town gas	Town gas plant	N/A
30-Dec-21	Sunny	OP10	15:12	21.6	1.8	Е	Yes	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature (oC)	Wind Speed (m/s)	Wind Direction	From Project Site	Odour Intensity	Odour Characteristic	Possible Source	Remarks
30-Dec-21	Sunny	OP11	15:23	21.1	1.5	Е	No	0	N/A	N/A	N/A
30-Dec-21	Fine	OP1	18:00	18.2	0.6	NW	Yes	0	N/A	N/A	N/A
30-Dec-21	Fine	OP2	18:03	18.1	0.4	Ν	Yes	0	N/A	N/A	N/A
30-Dec-21	Fine	OP3	18:07	17.3	1.6	W	Yes	0	N/A	N/A	N/A
30-Dec-21	Fine	OP4	18:11	17.0	3.0	Е	No	0	N/A	N/A	N/A
30-Dec-21	Fine	OP5	18:15	17.1	1.3	Е	No	0	N/A	N/A	N/A
30-Dec-21	Fine	OP6	18:19	16.9	1.5	Е	Yes	0	N/A	N/A	N/A
30-Dec-21	Fine	OP7	18:22	16.8	1.1	Ν	Yes	0	N/A	N/A	N/A
30-Dec-21	Fine	OP8	18:25	16.9	0.5	Ν	Yes	0	N/A	N/A	N/A
30-Dec-21	Fine	OP9	18:29	16.7	1.7	Ν	No	0	N/A	N/A	N/A
30-Dec-21	Fine	OP10	18:34	16.8	1.4	Ν	No	0	N/A	N/A	N/A
30-Dec-21	Fine	OP11	18:45	16.7	0.8	W	Yes	0	N/A	N/A	N/A
31-Dec-21	Overcast	OP1	10:50	18.8	0.9	Ν	Yes	0	N/A	N/A	N/A
31-Dec-21	Overcast	OP2	10:54	18.3	1.3	S	No	0	N/A	N/A	N/A
31-Dec-21	Overcast	OP3	10:59	18.0	1.2	Ν	Yes	1	Oil	Generator	N/A
31-Dec-21	Overcast	OP4	11:04	18.1	3.1	Е	No	1	Oil	Vehicle	N/A
31-Dec-21	Overcast	OP5	11:08	18.8	2.8	Е	No	0	N/A	N/A	N/A
31-Dec-21	Overcast	OP6	11:11	18.5	2.1	Ν	No	0	N/A	N/A	N/A
31-Dec-21	Overcast	OP7	11:15	18.1	1.9	Ν	Yes	0	N/A	N/A	N/A
31-Dec-21	Overcast	OP8	11:19	17.9	2.1	Е	Yes	0	N/A	N/A	N/A
31-Dec-21	Overcast	OP9	11:23	18.7	0.7	Ν	No	0	N/A	N/A	N/A
31-Dec-21	Overcast	OP10	11:27	18.1	2.2	Ν	No	0	N/A	N/A	N/A
31-Dec-21	Overcast	OP11	11:38	18.0	1.9	Е	No	0	N/A	N/A	N/A
31-Dec-21	Sunny	OP1	14:40	20.9	0.5	S	No	0	N/A	N/A	N/A
31-Dec-21	Sunny	OP2	14:43	18.4	3.6	S	No	0	N/A	N/A	N/A
31-Dec-21	Sunny	OP3	14:46	19.0	1.9	SW	No	0	N/A	N/A	N/A
31-Dec-21	Sunny	OP4	14:48	19.9	1.3	SE	No	0	N/A	N/A	N/A
31-Dec-21	Sunny	OP5	14:51	20.1	2.8	NE	Yes	0	N/A	N/A	N/A
31-Dec-21	Sunny	OP6	14:53	20.6	0.8	S	No	0	N/A	N/A	N/A
31-Dec-21	Sunny	OP7	14:56	20.5	1.1	S	No	0	N/A	N/A	N/A
31-Dec-21	Sunny	OP8	14:59	20.3	1.0	SW	No	1	Exhaust Gas	Vehicle	N/A
31-Dec-21	Sunny	OP9	15:03	21.0	1.0	S	No	0	N/A	N/A	N/A
31-Dec-21	Sunny	OP10	15:05	19.7	1.1	S	No	0	N/A	N/A	N/A
31-Dec-21	Sunny	OP11	15:13	19.7	1.9	SE	No	0	N/A	N/A	N/A
31-Dec-21	Fine	OP1	18:05	15.6	1.5	Ν	Yes	0	N/A	N/A	N/A
31-Dec-21	Fine	OP2	18:08	15.7	0.6	N	Yes	0	N/A	N/A	N/A
31-Dec-21	Fine	OP3	18:11	15.4	0.9	SE	No	0	N/A	N/A	N/A
31-Dec-21	Fine	OP4	18:15	15.3	1.0	W	No	0	N/A	N/A	N/A

Date	Weather	Location	Time	Temperature	Wind Speed	Wind	From	Odour	Odour	Possible Source	Remarks
				(oC)	(m/s)	Direction	Project Site	Intensity	Characteristic		
31-Dec-21	Fine	OP5	18:19	15.1	1.4	Е	No	0	N/A	N/A	N/A
31-Dec-21	Fine	OP6	18:23	15.0	1.3	Ν	Yes	0	N/A	N/A	N/A
31-Dec-21	Fine	OP7	18:26	15.2	1.1	W	No	0	N/A	N/A	N/A
31-Dec-21	Fine	OP8	18:30	15.3	1.7	Е	Yes	0	N/A	N/A	N/A
31-Dec-21	Fine	OP9	18:34	15.4	1.5	SE	Yes	0	N/A	N/A	N/A
31-Dec-21	Fine	OP10	18:38	15.5	0.5	Е	Yes	0	N/A	N/A	N/A
31-Dec-21	Fine	OP11	18:49	15.2	1.5	Ν	No	0	N/A	N/A	N/A

Annex D5

Thermal Oxidizer, Landfill Gas Flare and Landfill Gas Generator Stack Emission Monitoring Results

Parameters	Monitoring Results	
NO <sub>2</sub>	0.38 gs <sup>-1</sup>	
CO	<0.02 gs <sup>-1</sup>	
SO <sub>2</sub>	<0.01 gs <sup>-1</sup>	
Benzene	<2 x 10 <sup>-5</sup> gs <sup>-1</sup>	
Vinyl chloride	<2 x 10 <sup>-5</sup> gs <sup>-1</sup>	
Exhaust gas velocity	15.3 ms <sup>-1</sup>	

#### Table D5.1 Thermal Oxidiser Stack Emission Monitoring Results

#### Table D5.2 Thermal Oxidiser Stack Continuous Monitoring Results

Date	Gas Combustion		Exhaust temperature	Exhaust gas velocity	
		Temperature (°C)	(K)	(ms-1) (a)	
01 Dec 21		945	1235		
02 Dec 21		938	1226		
03 Dec 21		984	1316		
04 Dec 21		941	1264		
05 Dec 21		941	1223		
06 Dec 21		944	1237		
07 Dec 21		936	1238		
08 Dec 21		939	1234		
09 Dec 21		949	1253		
10 Dec 21		955	1270		
11 Dec 21		936	1230		
12 Dec 21		932	1231		
13 Dec 21		948	1219		
14 Dec 21		952	1272		
15 Dec 21		942	1226	15.3	
16 Dec 21		937	1222		
17 Dec 21		936	1224		
18 Dec 21		957	1221		
19 Dec 21		941	1226		
20 Dec 21		944	1230		
21 Dec 21		938	1241		
22 Dec 21		942	1219		
23 Dec 21		943	1230		
24 Dec 21		935	1223		
25 Dec 21		938	1229		
26 Dec 21		937	1223		
27 Dec 21		967	1287		
28 Dec 21		936	1223		
29 Dec 21		936	1225		
30 Dec 21		937	1221		
31 Dec 21		941	1228		
	Average	943	1237	-	
	Min		1219	-	
	Max	984	1316	-	

#### Notes:

(a) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring.

Table D5.3	Landfill Gas Flare Stack Emission Monitoring Results
------------	--

Parameters	Monitoring Results		
NO <sub>2</sub>	<0.02 gs <sup>-1</sup>		
СО	2.81 gs <sup>-1</sup>		
SO <sub>2</sub>	0.11 gs <sup>-1</sup>		
Benzene	9.9 x 10 <sup>-5</sup> gs <sup>-1</sup>		
Vinyl chloride	<1.4 x 10 <sup>-5</sup> gs <sup>-1</sup>		
Exhaust gas velocity	9.1 ms <sup>-1</sup>		

### Table D5.4Landfill Gas Flare Stack Continuous Monitoring Results

Date	Temperature	Exhaust temperature (K)	Exhaust gas velocity (ms <sup>-1</sup> ) <sup>(a)</sup>	Operation Status	
Flare 1 – F60	<u>(°C)</u> 1				
01 Dec 21	-	-		Standby	
02 Dec 21	935	1115		In Operation	
02 Dec 21 03 Dec 21	-	-		Standby	
05 Dec 21 04 Dec 21	-	_		Standby	
04 Dec 21 05 Dec 21	-	_		Standby	
05 Dec 21 06 Dec 21				Standby	
00 Dec 21 07 Dec 21				Standby	
07 Dec 21 08 Dec 21	-	-		Standby	
00 Dec 21 09 Dec 21	-	-		Standby	
10 Dec 21	-	-			
10 Dec 21 11 Dec 21	-	-		Standby Standby	
11 Dec 21 12 Dec 21	-	-		5	
	-	-		Standby	
13 Dec 21	850	1053	0.1	In Operation	
14 Dec 21	864	1047	9.1	In Operation	
15 Dec 21	854	1049		In Operation	
16 Dec 21	820	1025		In Operation	
17 Dec 21	-	-		Standby	
18 Dec 21	-	-		Standby	
19 Dec 21	-	-		Standby	
20 Dec 21	-	-		Standby	
21 Dec 21	-	-		Standby	
22 Dec 21	-	-		Standby	
23 Dec 21	-	-		Standby	
24 Dec 21	-	-		Standby	
25 Dec 21	-	-		Standby	
26 Dec 21	-	-		Standby	
27 Dec 21	-	-		Standby	
28 Dec 21	859	1064		In Operation	
29 Dec 21	-	-		Standby	
30 Dec 21	-	-		Standby	
31 Dec 21	-	-		Standby	
Average	864	1059	-		
Min	820	1025	-		
Max	935	1115	-		
Flare 2 – F60	2				
01 Dec 21	892	984		In Operation	
02 Dec 21	893	1097		In Operation	
03 Dec 21	890	1053		In Operation	
04 Dec 21	869	1065		In Operation	
05 Dec 21	878	1085		In Operation	
06 Dec 21	-	-		Standby	
07 Dec 21	-	-		Standby	
				J	

ENVIRONMENTAL RESOURCES MANAGEMENT

Date	Gas Combustion	Exhaust temperature	Exhaust gas	<b>Operation Status</b>
	Temperature	(K)	velocity (ms <sup>-1</sup> ) <sup>(a)</sup>	
	(°C)			
08 Dec 21	849	1016		In Operation
09 Dec 21	-	-		Standby
10 Dec 21	-	-		Standby
11 Dec 21	854	1037		In Operation
12 Dec 21	820	1045		In Operation
13 Dec 21	875	1078		In Operation
14 Dec 21	825	1027		In Operation
15 Dec 21	832	1026		In Operation
16 Dec 21	837	1038	9.1	In Operation
17 Dec 21	834	1014		In Operation
18 Dec 21	836	1079		In Operation
19 Dec 21	841	1078		In Operation
20 Dec 21	882	1007		In Operation
21 Dec 21	828	1038		In Operation
22 Dec 21	847	990		In Operation
23 Dec 21	829	976		In Operation
24 Dec 21	-	-		Standby
25 Dec 21	874	959		In Operation
26 Dec 21	857	949		In Operation
27 Dec 21	832	1025		In Operation
28 Dec 21	-	-		Standby
29 Dec 21	894	1040		In Operation
30 Dec 21	823	1021		In Operation
31 Dec 21	832	944		In Operation
Average	853	1027	-	
Min	820	944	-	
Max	894	1097	-	

#### Notes:

(a) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring.

#### Table D5.5Landfill Gas Generator Stack Emission Monitoring Results

Parameters	Monitoring Results		
NO <sub>2</sub>	0.007 gs <sup>-1</sup>		
СО	0.046 gs <sup>-1</sup>		
SO <sub>2</sub>	0.074 gs <sup>-1</sup>		
Benzene	$4 \ge 10^{-6} \text{ gs}^{-1}$		
Vinyl chloride	<1.2 x 10 <sup>-6</sup> gs <sup>-1</sup>		
Exhaust gas velocity	17.6 ms <sup>-1</sup>		

### Table D5.6Landfill Gas Generator Stack Continuous Monitoring Results

Date	Exhaust	Exhaust gas velocity	<b>Operation Status (Landfill Gas</b>
	temperature (K)	$(ms^{-1})^{(a)}$	Generator in Operation)
01 Dec 21	837		In Operation (ENGB)
02 Dec 21	837		In Operation (ENGB)
03 Dec 21	838		In Operation (ENGB)
04 Dec 21	843		In Operation (ENGB)
05 Dec 21	841		In Operation (ENGB)
06 Dec 21	843		In Operation (ENGB)
07 Dec 21	843		In Operation (ENGB)
08 Dec 21	844		In Operation (ENGB)
09 Dec 21	843		In Operation (ENGB)
10 Dec 21	847		In Operation (ENGA)
11 Dec 21	847	17.6	In Operation (ENGB)
12 Dec 21	843		In Operation (ENGB)
13 Dec 21	-		Under maintenance
14 Dec 21	843		In Operation (ENGB)
15 Dec 21	845		In Operation (ENGB)
16 Dec 21	846		In Operation (ENGB)
17 Dec 21	748		In Operation (ENGA)
18 Dec 21	-		Under maintenance
19 Dec 21	-		Under maintenance
20 Dec 21	842		In Operation (ENGB)
21 Dec 21	844		In Operation (ENGB)
22 Dec 21	841		In Operation (ENGB)
23 Dec 21	841		In Operation (ENGB)
24 Dec 21	841		In Operation (ENGB)
25 Dec 21	840		In Operation (ENGB)
26 Dec 21	838		In Operation (ENGB)
27 Dec 21	838		In Operation (ENGB)
28 Dec 21	838		In Operation (ENGB)
29 Dec 21	840		In Operation (ENGB)
30 Dec 21	841		In Operation (ENGB)
31 Dec 21	840		In Operation (ENGB)
Average	838	-	
Min		-	
Max	847	-	

#### Notes:

(a) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring.

Annex D6

Investigation Reports of Environmental Quality Limit Exceedance

Project	South East New Territories (SENT) Landfill Extension
Date	13 December 2021
Time	9:00 (13 December 2021) – 9:00 (14 December 2021)
Monitoring Location	AM4
Parameter	24-hour Total Suspended Particulates (TSP)
Action / Limit Levels	Action level: >260 $\mu$ g/ m <sup>3</sup>
	Limit level: >260 $\mu$ g/m <sup>3</sup>
Measured Level	$282 \mu g /m^3$
Measured Level Possible reason	From the meteorological data obtained from the SENTX on-site meteorological monitoring station, a predominantly easterly to east-southeasterly wind with highest wind speed 7.8m/s was recorded on 13 and 14 December 2021 during the sampling event. Occasional westerly to west-northwesterly wind was also recorded during the sampling event On 13 December 2021, dust emission from the public fill stockpiling areas and traffic emission from other project site n vicinity and located at the west of dust monitoring location AM4 were observed. The sample taken at AM4 on the day might not represent the operation dust emission from SENTX. In addition, no works which may lead to potential dust emission was conducted in the vicinity of dust monitoring location AM4 on the sampling day based on on-site observations and construction and operation activities as described by the Contractor. Environmental deficiency was not observed during the weekly site inspection on 9 December 2021. The Contractor has implemented the dust control and mitigation measures recommended in the updated EM&A Manual. In accordance with Table 3.8b of the updated EM&A Manual, repeat measurement was conducted on 19 December 2021 to confirm findings. 24-hour TSP level of 129 µg/m <sup>3</sup> (below Action
	and Limit Levels) was measured during the sampling event, which demonstrate no consecutive dust impact at AM4.
	Due to presence of the influencing factor other project sites and no potential source from the Project-related activities in the vicinity of AM4 which may lead to the high TSP level was identified, there is no adequate evidence showing that the TSP exceedance at AM4 was deemed to Project-related activities.
Action Taken / Action to be Taken	Examination of environmental performance of the Project will be continued during the weekly inspections. The Contractor is reminded to implement relevant and appropriate mitigation

### Investigation Report of Environmental Quality Limit Exceedance

		measures according to the updated EM&A Manual to avoid any exceedance of the Action and Limit Levels. In addition, the Contractor was reminded to discuss the dust control measures with CEDD to minimize the dust impact from
		other project site to the SENTX boundary.
Remarks		-
Prepared by:	Abbey Lau	
Designation:	Environmenta	1 Team
Date:	10 January 202	22

Project	South East New Territories (SENT) Landfill Extension
Date	17 December 2021
Time	11:00 - 11:30
Monitoring Location	Landfill Gas Flare 2 (F602)
Parameter	Carbon Monoxide (CO)
Limit Levels	>2.43 g/s
Measured Level	2.81 g/s
Possible reason	As confirmed by the Contractor, Landfill Gas Flare 2 (F602) was under normal operating conditions during the sampling event. The landfill gas flare emission monitoring results (NO <sub>2</sub> , SO <sub>2</sub> , Benzene, Vinyl chloride, gas combustion temperature, exhaust temperature and exhaust gas velocity) at Landfill Gas Flare 2 (F602) on 17 December 2021 were well within the respective limit levels. It is possible that the slight exceedance of CO limit level measured on 17 December 2021 could be due to some short-term system instability (e.g. insufficient air, short gas residence time or ineffective mixing of landfill gas and air during the combustion) during the sampling event. Hence, the CO exceedance at Landfill Gas Flare 2 (F602) on 17 December 2021 is considered to be Project related.
	In accordance with Table 3.8b of the updated EM&A Manual, repeat measurement was conducted on 12 January 2022 (it should be noted that the turnaround time of the laboratory analysis of the flue gas sample is 3 weeks and the results were available on 11 February 2022) to confirm findings. The CO concentration (0.032 g/s) measured on 12 January 2022 is well below Limit Level. There is no consecutive exceedance of CO concentrations in the flue gas emission of Landfill Gas Flare 2 (F602).
	It should also be noted that although the measured CO level exceeded the limit level of the EM&A programme (which was set based on the stack design parameters), the slight exceedance of CO on 17 December 2021 will not cause adverse air quality impact to the identified ASRs as the anticipated CO concentrations at the identified ASRs will still be well below the respective AQO criteria with reference to the findings of the operational air quality impact assessment of the SENTX Environmental Review Report.
Action Taken / Action to be Taken	Examination of environmental performance of the Project will be continued during the weekly inspections. The Contractor is reminded to closely monitoring the operating conditions of the flare to avoid any exceedance of the Action and Limit Levels.

### Investigation Report of Environmental Quality Limit Exceedance

Remarks	-	
Prepared by:	Abbey Lau	
Designation:	Environmental Tean	m
Date:	22 February 2022	

Annex E

### Noise


Annex E1

Noise Monitoring Results

Date	Start Time	Finish Time	Weather	L <sub>10 (30min)</sub>	L90 (30min)	Leq (30min)
7 Oct 21	14:37	15:07	Sunny	58.5	52.0	56.4
15 Oct 21	NA	NA	Drizzle	Monitori	ing was cance	lled due to
				a	dverse weath	ier.
21 Oct 21	15:05	15:35	Cloudy	56.0	52.5	54.5
28 Oct 21	14:43	15:13	Sunny	51.8	46.7	49.7
4 Nov 21	14:33	15:03	Sunny	53.5	48.0	52.5
11 Nov 21	15:08	15:38	Sunny	50.5	46.1	49.0
18 Nov 21	14:40	15:10	Sunny	52.5	46.3	50.6
25 Nov 21	14:49	15:19	Sunny	54.9	50.1	53.4
2 Dec 21	15:49	16:19	Sunny	50.5	48.0	49.7
9 Dec 21	15:21	15:51	Sunny	48.0	44.0	47.0
14 Dec 21	11:04	11:34	Sunny	52.2	49.8	51.0
22 Dec 21	15:36	16:06	Sunny	52.0	47.5	50.9
28 Dec 21	13:39	14:09	Sunny	52.5	49.0	51.1
					Average	e 51.3
					Mir	<b>n</b> 47.0
					Max	<b>x</b> 56.4

# Table E1.1Measured Noise Levels (dB(A)) at NM1 during Normal Working Hours (0700-<br/>1900 hours; Normal Weekdays)

#### Figure E1.1 Graphical Presentation for Noise Monitoring at NM1

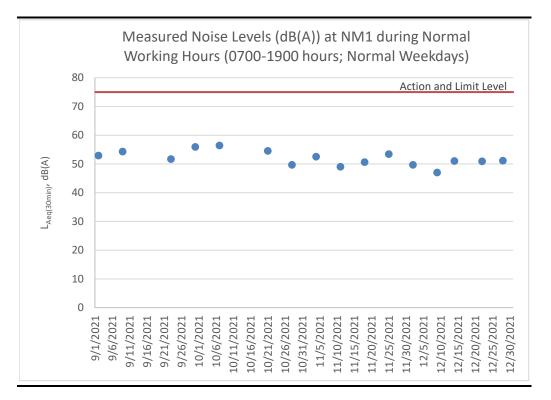

Annex E2

# Event and Action Plan for Noise Monitoring

Event		Action	
	ET	IEC	Contractor
Action Level	<ul> <li>Identify the source(s) and investigate the cause(s) of exceedance and complaint</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Have additional monitoring if exceedance is due to the Project. If exceedance stops, cease additional monitoring</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Submit proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> </ul>
	<ul> <li>Identify the source(s) and investigate the cause(s) of exceedance and complaint</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD whether the cause of exceedance is due to the Project</li> <li>Analyse the operation of SENTX and investigate the causes of exceedance</li> <li>Provide interim report to Contractor, IEC, Project Proponent and EPD the causes of the exceedances</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Report the remedial measures implemented and the additional monitoring results to Contactor, IEC, Project Proponent and EPD</li> <li>Have additional monitoring if exceedance is due to the Project. If exceedance stops, cease additional monitoring</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Take immediate measures to avoid further exceedance</li> <li>Submit proposals for remedial measures to IEC within 3 working days of notification</li> <li>Implement the agreed proposals</li> <li>Resubmit proposals if problem still not under control</li> <li>Stop the relevant activity of works as determined by the Project Proponent until the exceedance is abated</li> </ul>

### Annex E2 Event and Action Plan for Construction and Operational Noise Monitoring

Annex F

## Water Quality

Annex F1

# Surface Water Quality Monitoring Results

Date	Time	Weather	Water	Water	Water	Dissolved	pН	Suspended	Remarks
		Condition	Appearance	Condition	Temperature	Oxygen (DO)		Solids (SS)	
					(°C)	(mg/L)		(mg/L)	
7 Oct 21	14:23	Sunny		Unable to	collect water samp	le due to insuffic	ient flow		-
15 Oct 21	10:39	Rainy		Unable to	collect water samp	le due to insuffic	ient flow		-
21 Oct 21	14:48	Cloudy		Unable to	collect water samp	le due to insuffic	ient flow		-
28 Oct 21	14:25	Sunny		Unable to	collect water samp	le due to insuffic	ient flow		-
4 Nov 21	14:18	Sunny		Unable to	collect water samp	le due to insuffic	ient flow		
11 Nov 21	14:18	Sunny	Light yellow	Semi clear	19.7	9.19	8.32	8.6	-
11 Nov 21	14:38	Sunny	Light yellow	Semi clear	19.3	9.21	7.96	8.7	DP4T (Duplicate)
18 Nov 21	15:20	Sunny		Unable to	collect water samp	le due to insuffic	ient flow		
					Averag	e 9.20	8.14	8.7	-
					Mi	<b>n</b> 9.19	7.96	8.6	-
					Ma	<b>x</b> 9.21	8.32	8.7	-
Notes: DP4	was tempo:	rary relocated t	to DP4 (Future, te	mporary) (i.e. D	PP4T) as an interim	discharge point	from the n	nonitoring event or	n 16 May 2019.

#### Table F1.1 Surface Water Quality Monitoring Results at DP4T (During Construction Phase)

#### Table F1.2 Surface Water Quality Monitoring Results at DP4T (During Operation Phase)

Date	Time	Weather Condition	Water Appearance	Water Condition	Water Temperature (oC)	Ammoniacal- nitrogen (mg/L)	COD	Suspended Solids (SS) (mg/L)	Remarks
25 Nov 21	15:33	Sunny		Unable to o	collect water sam	ple due to insuffi	cient flow		-
28 Dec 21	10:46	Sunny		Unable to o	collect water sam	ple due to insuffi	cient flow		-
					Average	-	-	-	-
					Min	-	-	-	-
					Max	-	-	-	-


Date	Time	Weather Condition	Water Appearance	Water Condition	Water Temperature	Dissolved Oxygen (DO)	pН	Suspended Solids (SS)	Remarks
			11		(°C)	(mg/L)		(mg/L)	
7 Oct 21	14:08	Sunny		Unable to	collect water samp	le due to insuffici	ent flow		-
15 Oct 21	11:02	Rainy		Unable to	collect water samp	le due to insuffici	ent flow		-
21 Oct 21	14:42	Cloudy		Unable to	collect water samp	le due to insuffici	ent flow		-
28 Oct 21	14:16	Sunny		Unable to	collect water samp	le due to insuffici	ent flow		-
4 Nov 21	14:00	Sunny		Unable to	collect water samp	le due to insuffici	ent flow		-
11 Nov 21	14:10	Sunny		Unable to	collect water samp	le due to insuffici	ent flow		-
18 Nov 21	15:16	Sunny		Unable to	collect water samp	le due to insuffici	ent flow		-
					Averag	e -	-	-	-
					Min	n -	-	-	-
					Ma	x -	-	-	-

 Table F1.3
 Surface Water Quality Monitoring Results at DP6 (During Construction Phase)


 Table F1.4 Surface Water Quality Monitoring Results at DP6 (During Operation Phase)


Date	Time	Weather Condition	Water Appearance	Water Condition	Water Temperature (oC)	Ammoniacal- nitrogen (mg/L)	COD	Suspended Solids (SS) (mg/L)	Remarks
25 Nov 21	15:17	Sunny		Unable to d	collect water san	ple due to insuffi	cient flow		-
28 Dec 21	10:42	Sunny		Unable to d	collect water san	ple due to insuffi	cient flow		-
					Average	2 -	-	-	-
					Mir	1 -	-	-	-
					May	K -	-	-	-

# Figure F1.1 Graphical Presentation for Surface Water Quality Monitoring (DO) (During Construction Phase)

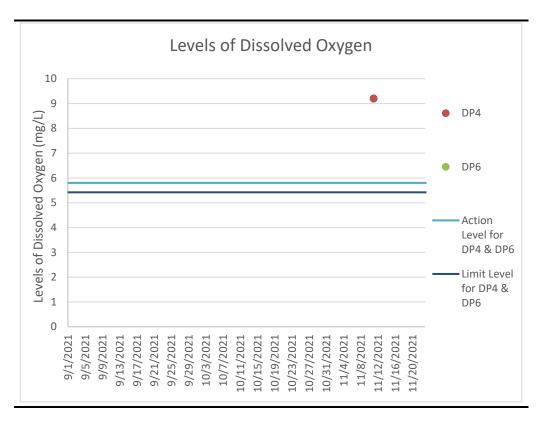

*Figure F1.2 Graphical Presentation for Surface Water Quality Monitoring (pH) (During Construction Phase)* 

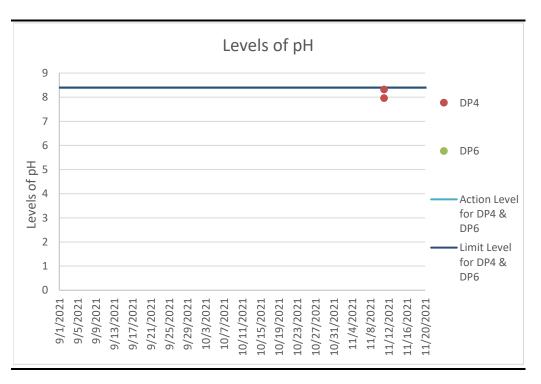

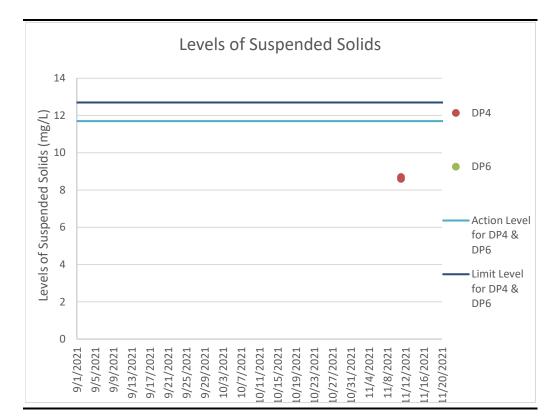

# Figure F1.3 Graphical Presentation for Surface Water Quality Monitoring (SS) (During Construction Phase)

Annex F2

# Event and Action Plan for Water Quality Monitoring

Event		Action	
	ET	IEC	Contractor
Action Level being exceeded by one ampling day	<ul> <li>Repeat <i>in situ</i> measurement to confirm findings</li> <li>Identify the source(s) and investigate the cause(s) of exceedance</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project</li> <li>Repeat measurement on the next day of exceedance if exceedance is due to the Project</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working methods</li> </ul>	<ul> <li>Rectify any unacceptable practice</li> <li>Amend working methods if appropriate</li> </ul>
Action Level being exceeded by two consecutive ampling days	<ul> <li>Repeat <i>in situ</i> measurement to confirm findings</li> <li>Identify the source(s) and investigate the cause(s) of exceedance</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Increase the monitoring frequency to daily if exceedance is due to the Project and continue until no exceedance of Action Level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working methods</li> <li>Discuss with ET Leader and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Submit proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate</li> </ul>

### Annex F2a Event and Action Plan for Surface Water Quality During Construction Phase

Event	Action								
	ET	IEC	Contractor						
Limit Level being exceeded by two consecutive sampling days	<ul> <li>Repeat <i>in situ</i> measurement to confirm findings</li> <li>Identify source(s) of impact and cause(s) of exceedance</li> <li>Prepare the Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Increase the monitoring frequency to daily if exceedance is due to the Project until no exceedance of Limit Level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working methods</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Critically review the working methods</li> <li>Rectify unacceptable practice</li> <li>Check all plant and equipment</li> <li>Consider changes of working methods</li> <li>Discuss with the ET and IEC and propose mitigation measures to the IEC</li> <li>Implement the agreed mitigation measures</li> </ul>						
Limit Level being exceeded by more than two consecutive sampling days	<ul> <li>Repeat <i>in situ</i> measurement to confirm findings</li> <li>Identify source(s) of impact and cause(s) of exceedance</li> <li>Prepare the Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Check monitoring data, all plant, equipment and Contractor's working methods</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure mitigation measures are implemented</li> <li>Increase the monitoring frequency to daily if exceedance is due to the Project until no exceedance of Limit Level for two consecutive days</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working methods</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Critically review the working methods</li> <li>Rectify unacceptable practice</li> <li>Check all plant and equipment</li> <li>Consider changes of working methods</li> <li>Discuss with the ET and IEC and propose mitigation measures</li> <li>Implement the agreed mitigation measure</li> <li>As directed by the Project Proponent, slow down or stop all or part of the construction activities</li> </ul>						

Event		Action	
	ET	IEC	Contractor
xceedance of imit Level for urface water nonitoring	<ul> <li>Identify source(s) of impact and investigate the cause(s) of exceedance</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Repeat measurement to confirm finding if exceedance is due to the Project</li> <li>Increase monitoring frequency to weekly if exceedance is due to the Project until no exceedance of Limit Level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working methods</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Take immediate action to avoid further exceedance</li> <li>Submit proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate</li> </ul>
Exceedance of Limit Level for groundwater monitoring	<ul> <li>Identify source(s) of impact and investigate the cause(s) of exceedance</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Repeat measurement to confirm finding if exceedance is due to the Project</li> <li>Increase monitoring frequency to weekly if exceedance is due to the Project until no exceedance of Limit Level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check monitoring data submitted by ET</li> <li>Check Contractor's working methods</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Divert groundwater collected at the collection sumps to the leachate treatment plant</li> <li>Submit proposals for remedial measures to IEC</li> <li>Rectify any unacceptable practice or design</li> <li>Amend working methods as required</li> <li>Implement amended working methods, if necessary</li> </ul>

### Annex F2b Event and Action Plan for Water Quality Monitoring During Operation/Restoration Phase

Event	Action									
	ET	IEC	Contractor							
Exceedance of Limit Level for leachate level	<ul> <li>Investigate the cause(s) of exceedance</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check with Contractor on the operating activities and performance of the leachate collection system</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Check the performance of the leachate collection system</li> <li>Rectify any unacceptable practice;</li> <li>Amend leachate collection design if required</li> <li>Implement amended leachate collection system, if necessary</li> </ul>							
Exceedance of Limit Level of effluent discharge from LTP	<ul> <li>Investigate the cause(s) of exceedance</li> <li>Prepare Notification of Exceedance within 24 hours</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Repeat measurement to confirm finding if exceedance is due to the Project</li> <li>Increase monitoring frequency to weekly until no exceedance of Limit Level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Check with Contractor on the operation performance of the LTP</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Rectify any unacceptable practice;</li> <li>Carry out remedial measures or amend design as required</li> <li>Implement amended design, if necessary</li> </ul>							

Annex F3

### Leachate Levels Monitoring Results

Date	Meter No.X1 (cm)	Meter No.X2 (cm)	Average (cm)
Pump Station No.		. ,	<u> </u>
21 Nov 21	79	99	89
22 Nov 21	79	99	89
23 Nov 21	79	99	89
24 Nov 21	79	99	89
25 Nov 21	44	64	54
26 Nov 21	46	66	56
27 Nov 21	50	70	60
28 Nov 21	50	70	60
29 Nov 21	50	70	60
30 Nov 21	50	70	60
01 Dec 21	53	73	63.0
02 Dec 21	53	73	63.0
03 Dec 21	53	73	63.0
04 Dec 21	55	75	65.0
05 Dec 21	57	75	66.0
06 Dec 21	57	75	66.0
07 Dec 21	57	77	67.0
08 Dec 21	57	75	66.0
09 Dec 21	86	10	48.0
10 Dec 21	84	102	93.0
11 Dec 21	84	104	94.0
12 Dec 21	90	111	100.5
13 Dec 21	111	90	100.5
14 Dec 21	62	82	72.0
15 Dec 21	68	82	75.0
16 Dec 21	64	84	74.0
17 Dec 21	64	84	74.0
18 Dec 21	66	86	76.0
19 Dec 21	88	68	78.0
20 Dec 21	88	68	78.0
21 Dec 21	70	91	80.5
22 Dec 21	44	64	54.0
23 Dec 21	46	66	56.0
24 Dec 21	46	66	56.0
25 Dec 21	53	73	63.0
26 Dec 21	53	73	63.0
27 Dec 21	53	73	63.0
28 Dec 21	55	75	65.0
29 Dec 21	57	77	67.0
30 Dec 21	59	79	69.0
31 Dec 21	82	100	91.0
Aver	<b>age</b> 64	78	71
	<b>Min</b> 44	10	48
N	<b>Max</b> 111	111	101

#### Table F3.1Leachate Levels Monitoring Results (Pump Station No.1X (Cell 1X))


Date	Meter No.X1 (cm)	Meter No.X2 (cm)	Average (cm)		
Pump Station N	o. 2X (Cell 2X)				
10 Dec 21	84	82	83.0		
11 Dec 21	88	86	87.0		
12 Dec 21	88	86	87.0		
13 Dec 21	88	86	87.0		
14 Dec 21	88	86	87.0		
15 Dec 21	88	86	87.0		
16 Dec 21	88	86	87.0		
17 Dec 21	88	86	87.0		
18 Dec 21	88	86	87.0		
19 Dec 21	70	73	71.5		
20 Dec 21	70	73	71.5		
21 Dec 21	84	88	86.0		
22 Dec 21	79	82	80.5		
23 Dec 21	82	84	83.0		
24 Dec 21	73	75	74.0		
25 Dec 21	70	73	71.5		
26 Dec 21	70	73	71.5		
27 Dec 21	70	73	71.5		
28 Dec 21	75	77	76.0		
29 Dec 21	77	82	79.5		
30 Dec 21	82	84	83.0		
31 Dec 21	84	88	86.0		
Ave	erage 81	82	81		
	<b>Min</b> 70	73	72		
	<b>Max</b> 88	88	87		

#### Table F3.2Leachate Levels Monitoring Results (Pump Station No.2X (Cell 2X))


Table F3.3Leachate Levels Monitoring Results (Pump Station No.3X (Cell 3X))

Date	Meter No.X1 (cm)	Meter No.X2 (cm)	Average (cm)
Pump Station No. 3X	(Cell 3X)		
23 Dec 21	90	90	90.0
24 Dec 21	97	97	97.0
25 Dec 21	84	84	84.0
26 Dec 21	84	84	84.0
27 Dec 21	84	84	84.0
28 Dec 21	95	95	95.0
29 Dec 21	99	99	99.0
30 Dec 21	79	79	79.0
31 Dec 21	86	86	86.0
Average	89	89	89
Min	79	79	79
Max	99	99	99


## *Figure F3.1 Graphical Presentation for Leachate Levels Monitoring (Pump Station No.1X (Cell 1X))*

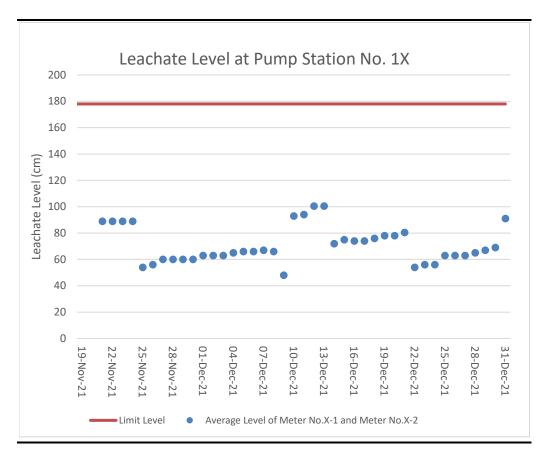

*Figure F3.2 Graphical Presentation for Leachate Levels Monitoring (Pump Station No.2X (Cell 2X))* 

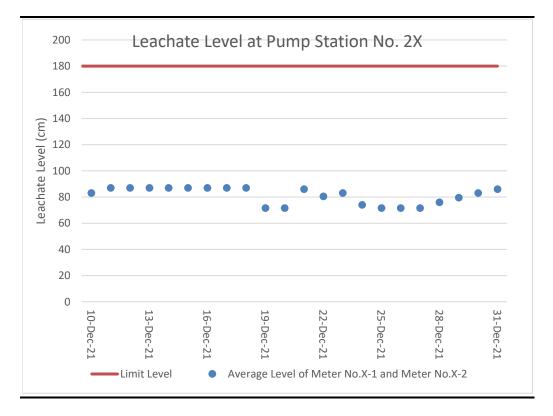

# *Figure F3.3 Graphical Presentation for Leachate Levels Monitoring (Pump Station No.3X (Cell 3X))*

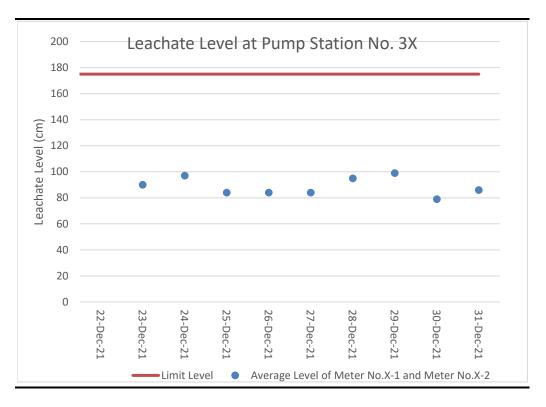

Annex F4

### Effluent Quality Monitoring Results

#### Table F4.1Effluent Monitoring Results

		21 Nov 2021	22 Nov 2021	23 Nov 2021	24 Nov 2021	25 Nov 2021	26 Nov 2021	27 Nov 2021	28 Nov 2021	29 Nov 2021	30 Nov 2021
<b>On-site Measurements</b>											
Temperature	°C	28.9	20.5	18.6	21.5	24.5	24.5	27.5	28.6	28.9	26.0
pH Value	pH Unit	8.4	8.4	8.5	8.4	8.4	8.4	8.5	8.4	8.4	8.3
Volume Discharged	m <sup>3</sup>	987	301	910	1462	1264	1207	1332	900	486	961
Laboratory Analysis											
Suspended Solids (SS)	mg/L	29.3	35.2	33.3	28.4	24.0	25.3	20.4	26.8	24.3	23.3
Alkalinity	mg/L	2060	2140	2130	2140	2120	2130	2130	2120	2100	2160
Ammoniacal-nitrogen	mg/L	0.33	0.49	0.3	0.3	0.28	0.36	0.31	0.33	0.32	0.84
Chloride	mg/L	1860	1820	2160	2230	2150	2210	2210	2220	2230	2160
Nitrite-nitrogen	mg/L	<0.10	0.38	0.04	0.15	0.05	<0.10	0.14	0.15	0.29	0.63
Phosphate	mg/L	9.36	9.8	10.1	9.52	9.2	9.6	9.66	9.38	9.67	10.3
Sulphate	mg/L	63	64	70	64	63	61	64	64	58	65
Total Nitrogen	mg/L	115	110	95.7	90.4	98	109	112	113	112	102
Nitrate-nitrogen	mg/L	68.5	65.8	50.5	46.4	53.3	64.6	66.8	67.8	69.6	54.6
Biochemical Oxygen											
Demand (BOD)	mg/L	10	13	12	11	14	10	12	8	6	7
Chemical Oxygen											
Demand (COD)	mg/L	904	888	888	970	921	929	937	1620	1090	1030
Oil & Grease	mg/L	<5	<5	<5	<5	<5	<5	<5	<5	<5	<5
Total Organic Carbon											
(TOC)	mg/L	324	332	345	362	368	422	358	346	381	392
Boron	µg/L	5130	5280	5450	5070	4900	5140	5260	5440	5500	5290
Calcium	mg/L	15.4	15.4	16	15.3	16.6	16.1	15.4	15.9	15.5	16.1
Iron	mg/L	1.28	1.36	1.53	1.56	1.47	1.37	1.32	1.43	1.32	1.45
Magnesium	mg/L	12.1	12.4	13.3	13	13.8	13.4	13	13.5	13.4	13.3
Potassium	mg/L	1070	1050	844	864	827	856	846	853	892	910
Cadmium	µg/L	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0
Chromium	µg/L	120	123	123	132	128	128	123	124	122	134
Copper	µg/L	<10	<10	<10	<10	<10	<10	11	<10	<10	<10
Nickel	µg/L	116	116	112	117	113	116	112	111	110	115
Zinc	µg/L	70	70	70	70	70	60	60	60	60	60

		1 Dec 21	2 Dec 21	3 Dec 21	4 Dec 21	5 Dec 21	6 Dec 21	7 Dec 21	8 Dec 21	9 Dec 21	10 Dec 21	11 Dec 21
<b>On-site Measurements</b>	3											
Temperature	°C	26.3	25.7	25.8	25.4	24.8	25.3	25.4	26.1	24.8	28.1	28.8
pH Value	pH Unit	8.4	8.4	8.4	8.4	8.4	8.4	8.4	8.4	8.4	8.4	8.4
Volume Discharged	m <sup>3</sup>	1264	1193	1225	667	791	663	1149	1249	1401	1293	1139
Laboratory Analysis		•										
Suspended Solids (SS)	mg/L	32.4	23	21.6	22.8	13.3	23.1	27.5	21.3	22.1	14.2	28
Alkalinity	mg/L	2200	2180	2120	2130	2130	2160	2160	2200	2190	2130	2110
Ammoniacal-nitrogen	mg/L	0.39	0.38	0.38	0.26	0.32	< 0.10	< 0.10	0.27	0.42	0.37	0.3
Chloride	mg/L	2200	1770	1780	1640	1710	1710	1680	1660	1760	1750	1770
Nitrite-nitrogen	mg/L	0.28	0.33	0.29	< 0.10	0.36	0.3	0.19	0.18	0.21	0.23	0.16
Phosphate	mg/L	10.2	9.28	10.2	10.5	9.27	10.1	10.3	9.7	9.58	9.98	9.89
Sulphate	mg/L	66	60	61	65	59	61	64	66	62	63	62
Total Nitrogen	mg/L	104	115	125	130	127	112	90.4	93.4	110	113	118
Nitrate-nitrogen	mg/L	53.5	58	73	80.3	79.6	64.1	43	44.3	54.6	61	65.8
Biochemical Oxygen		10	11	11	24	9	9	12	11	7	7	9
Demand (BOD)	mg/L											
Chemical Oxygen		1230	1380	838	889	1430	923	973	913	785	938	823
Demand (COD)	mg/L											
Oil & Grease	mg/L	<5	<5	<5	<5	<5	<5	<5	<5	<5	<5	<5
Total Organic Carbon		394	424	359	348	372	409	344	360	357	348	343
(TOC)	mg/L											
Boron	µg/L	5240	5440	4940	5240	5400	5180	5170	5030	5470	5170	4580
Calcium	mg/L	15.5	16.1	14.6	18.0	15.0	15.9	15.2	15.4	14.3	14.1	15.8
Iron	mg/L	1.51	1.58	1.33	1.67	1.51	1.74	1.65	1.43	1.41	1.37	1.44
Magnesium	mg/L	13.1	13.4	12.1	15.2	13.2	13.9	13.5	12.6	12.8	12.6	14
Potassium	mg/L	844	888	816	835	860	858	836	806	818	824	868
Cadmium	µg/L	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0
Chromium	µg/L	137	140	122	112	130	131	127	120	128	130	123
Copper	µg/L	<10	<10	<10	<10	<10	<10	<10	<10	<10	<10	<10
Nickel	µg/L	117	120	107	98	114	112	107	108	113	115	106
Zinc	μg/L	60	60	50	40	50	50	50	60	56	56	54

		12 Dec 21	13 Dec 21	14 Dec 21	15 Dec 21	16 Dec 21	17 Dec 21	18 Dec 21	19 Dec 21	20 Dec 21	21 Dec 21	22 Dec 21
<b>On-site Measurements</b>	3											
Temperature	°C	29.5	26.6	26.2	27.8	30.6	27.6	23.9	27.6	22	21.7	27.3
pH Value	pH Unit	8.4	8.4	8.5	8.4	8.4	8.4	8.3	8.4	8.4	8.5	8.4
Volume Discharged	m <sup>3</sup>	926	488	1170	1293	1201	1409	668	473	531	1195	1186
Laboratory Analysis												
Suspended Solids (SS)	mg/L	13.6	20.3	22.7	18.1	21.7	23.5	23.1	33.8	14.4	23.9	16.3
Alkalinity	mg/L	2120	2130	2190	2200	2210	2210	2200	2150	2160	2190	2170
Ammoniacal-nitrogen	mg/L	0.3	0.42	0.32	0.36	0.32	0.35	0.32	0.34	0.75	0.35	0.18
Chloride	mg/L	1780.0	1810	1860	2080	2090	1850	1850	1930	1960	1800	1770
Nitrite-nitrogen	mg/L	0.2	0.31	0.18	0.19	0.2	0.19	0.28	0.18	0.7	0.26	0.22
Phosphate	mg/L	9.8	10.6	10.4	10.4	10.7	10.3	10.8	10.9	11.2	11.5	10.5
Sulphate	mg/L	61.0	67	63	68	64	68	64	66	70	66	61
Total Nitrogen	mg/L	123.0	119	110	104	118	121	127	135	132	129	113
Nitrate-nitrogen	mg/L	72.5	67.5	56.7	54.8	65.8	68.9	74.4	77.4	76.2	74.2	64.1
Biochemical Oxygen		8	11	13	11	12	11	8	12	10	10	8
Demand (BOD)	mg/L											
Chemical Oxygen		804	880	938	900	919	1070	919	976	981	1050	1020
Demand (COD)	mg/L											
Oil & Grease	mg/L	<5	<5	<5	<5	<5	<5	<5	<5	<5	<5	<5
Total Organic Carbon		347.0	359	351	348	356	352	397	374	398	386	387
(TOC)	mg/L											
Boron	µg/L	4880.0	4660	4780	5040	5680	5540	5460	5590	5520	6050	5860
Calcium	mg/L	15.0	14.8	17.1	14.4	15	13.6	13.1	13.1	12.7	14.1	17.7
Iron	mg/L	1.3	1.42	1.54	1.29	1.35	1.32	1.28	1.41	1.26	1.53	1.56
Magnesium	mg/L	13.5	13.1	14.7	12.7	12.7	12.1	11.5	11.6	11.5	13.9	14.5
Potassium	mg/L	914.0	898	934	879	931	844	827	800	808	898	892
Cadmium	µg/L	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0
Chromium	µg/L	131.0	130	130	128	138	137	141	146	138	135	138
Copper	µg/L	<10	<10	<10	<10	<10	<10	<10	61	<10	<10	<10
Nickel	µg/L	115.0	112	112	112	119	121	123	122	116	115	116
Zinc	µg/L	56.0	59	58	55	61	56	57	100	48	54	62

		23 Dec 21	24 Dec 21	25 Dec 21	26 Dec 21	27 Dec 21	28 Dec 21	29 Dec 21	30 Dec 21	31 Dec 21
<b>On-site Measurements</b>	6									
Temperature	°C	25.8	25.7	20.7	23.3	20	22.6	27.6	28.9	26.2
pH Value	pH Unit	8.4	8.5	8.4	8.5	8.5	8.5	8.4	8.4	8.5
Volume Discharged	m <sup>3</sup>	934	957	1000	734	499	1120	1348	1435	1189
Laboratory Analysis		•								
Suspended Solids (SS)	mg/L	14.3	14	17.4	13.9	10.1	11.6	15.7	26	14.8
Alkalinity	mg/L	2110	2100	2120	2190	2190	2160	2200	2250	2210
Ammoniacal-nitrogen	mg/L	0.15	0.34	0.24	0.28	0.46	0.41	0.38	0.28	0.3
Chloride	mg/L	2030	2130	1880	1840	1950	1870	2070	2070	2050
Nitrite-nitrogen	mg/L	0.19	0.18	0.15	0.15	0.33	0.16	0.16	0.14	0.16
Phosphate	mg/L	9.85	9.8	10.2	9.33	10.1	10.2	8.2	7.67	8.56
Sulphate	mg/L	57	65	67	74	78	82	88	90	92
Total Nitrogen	mg/L	121	114	106	112	106	106	91.2	98.4	108
Nitrate-nitrogen	mg/L	70.7	57	56.5	54.5	54.3	53	42.4	47.6	57
Biochemical Oxygen		8	6	7	7	7	6	8	9	7
Demand (BOD)	mg/L									
Chemical Oxygen		1020	973	973	973	920	1130	1040	989	1010
Demand (COD)	mg/L									
Oil & Grease	mg/L	<5	<5	<5	<5	<5	<5	<5	<5	<5
Total Organic Carbon		338	340	368	362	394	340	335	359	388
(TOC)	mg/L									
Boron	µg/L	4530	4660	4700	4750	4950	4920	4810	4830	5350
Calcium	mg/L	17.5	16.8	14.6	15.9	14.9	16.1	17.6	17.6	17.8
Iron	mg/L	1.39	1.33	1.21	1.37	1.32	1.32	1.58	1.61	1.43
Magnesium	mg/L	13.6	13	11.3	13.8	14	15.4	21.2	22.1	20.3
Potassium	mg/L	854	865	759	847	857	848	885	885	824
Cadmium	µg/L	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0
Chromium	µg/L	124	120	128	124	124	119	127	130	125
Copper	µg/L	24	<10	<10	<10	<10	<10	<10	<10	<10
Nickel	µg/L	101	98	116	116	119	114	120	124	112
Zinc	µg/L	68	58	54	58	57	58	54	58	54

Annex F5

## Groundwater Monitoring Results

#### Table F5.1Groundwater Monitoring Results

Parameters	Units	MWX-1	MWX-2	MWX-3	MWX-4	MWX-5	MWX-6	MWX-7	MWX-8	MWX-9	MWX-10	MWX-11	MWX-12	MWX-13	MWX-14
Water Level	mPD	2.70	2.84	2.79	2.69	2.71	2.65	2.42	2.53	2.89	2.93	3.23	6.62	36.50	45.13
Bicarbonate Alkalinity as CaCO3	mg/L	138	309	147	<1	<1	<1	8	<1	75	167	135	60	15	8
Carbonate Alkalinity as CaCO3	mg/L	<1	<1	<1	100	98	164	58	75	10	<1	<1	<1	<1	<1
Total Alkalinity as CaCO3	mg/L	138	309	147	129	118	200	66	114	85	167	135	60	15	8
pH Value	pH Unit	8.3	7.9	8	10.7	10.6	10.8	9.8	10.7	8.6	7.9	8.1	7	5.5	5.3
Electrical Conductivity @ 25°C	μS/cm	747	799	1110	1110	1130	1160	2330	3050	1550	863	372	319	95	97
Ammonia as N	mg/L	0.29	0.02	1.33	6.79	1.95	3.52	5.42	12.5	5.34	0.03	0.02	< 0.01	0.04	< 0.01
Chloride	mg/L	116	29	197	246	193	177	681	1010	372	133	26	22	16	20
Nitrite as N	mg/L	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01
Reactive Phosphorus as P	mg/L	0.02	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	0.02	0.01	0.02	0.02	0.02	0.04	< 0.01	< 0.01
Sulphate as SO4 - Turbidimetric	mg/L	54	91	95	54	131	91	66	38	111	74	13	57	3	2
Sulphide as S2-	mg/L	0.1	< 0.1	< 0.1	7.7	3.1	9.6	1.8	11.8	0.3	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
Total Kjeldahl Nitrogen as N	mg/L	0.4	0.2	1.7	7.4	2.6	4.8	5.9	12.9	6	< 0.1	0.1	< 0.1	0.4	0.2
Nitrate as N	mg/L	< 0.01	0.35	< 0.01	< 0.01	< 0.01	< 0.01	0.01	0.01	< 0.01	< 0.01	< 0.01	< 0.01	0.12	0.1
Total Nitrogen as N	mg/L	0.4	0.5	1.7	7.4	2.6	4.8	5.9	12.9	6	< 0.1	0.1	< 0.1	0.5	0.3
Boron	µg/L	120	210	180	160	170	180	480	540	380	90	50	20	10	10
Calcium	mg/L	37.6	52.1	74.4	48.8	40.4	30.8	26.3	59.9	31.8	74.3	46.5	29.5	2.3	1.53
Mercury	µg/L	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20
Magnesium	mg/L	5.22	47.4	5.64	< 0.05	< 0.05	< 0.05	1.01	0.12	12.4	7.03	2.5	4.62	1.02	1.04
Sodium	mg/L	85.7	28.8	111	128	141	154	419	488	233	83.3	25	27	14.1	12.9
Iron	mg/L	< 0.04	< 0.04	0.21	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	0.38	< 0.04	< 0.04
Potassium	mg/L	20.1	9.99	27.8	34.6	51.9	55.9	57.8	54.8	36.9	11.4	6.45	3.21	4.25	4.06
Cadmium	µg/L	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2	<0.2	< 0.2	< 0.2	< 0.2	<0.2	< 0.2	<0.2	< 0.2	< 0.2
Chromium	µg/L	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1
Copper	μg/L	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	1	1
Lead	μg/L	<1	<1	<1	<1	<1	3	<1	<1	<1	<1	<1	<1	<1	<1
Manganese	μg/L	417	216	956	2	<1	<1	<1	<1	8	1090	363	800	36	9
Nickel	µg/L	<1	<1	<1	2	1	2	<1	1	<1	<1	<1	<1	<1	<1
Zinc	µg/L	<10	260	<10	<10	<10	<10	<10	<10	<10	<10	<10	360	20	<10
Biochemical Oxygen Demand	mg/L	<2	<2	<2	<2	<2	7	<2	8	2	<2	<2	<2	<2	<2
Chemical Oxygen Demand	mg/L	11	3	19	36	28	56	23	44	20	6	4	<2	<2	<2
Total Organic Carbon	mg/L	6	4	9	11	10	13	8	11	9	4	4	4	4	4

Figure F5.1 Graphical Presentation for Groundwater Monitoring (MWX-1)

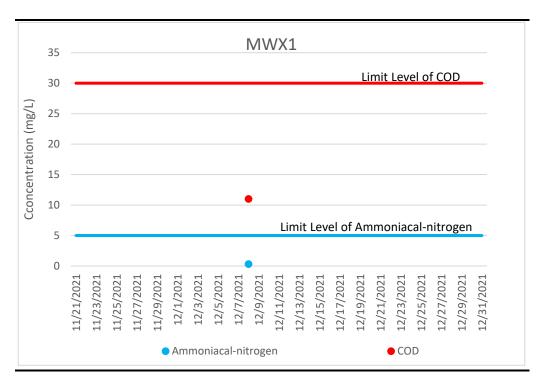


Figure F5.2 Graphical Presentation for Groundwater Monitoring (MWX-2)

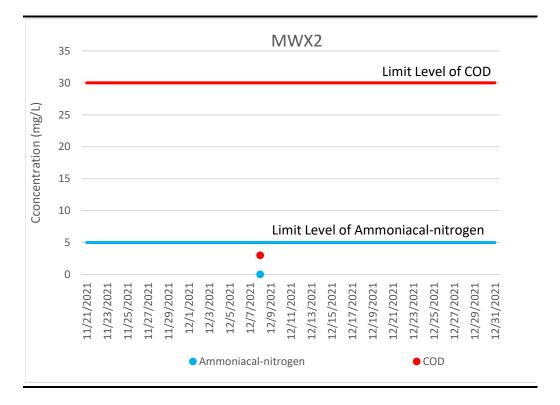


Figure F5.3 Graphical Presentation for Groundwater Monitoring (MWX-3)

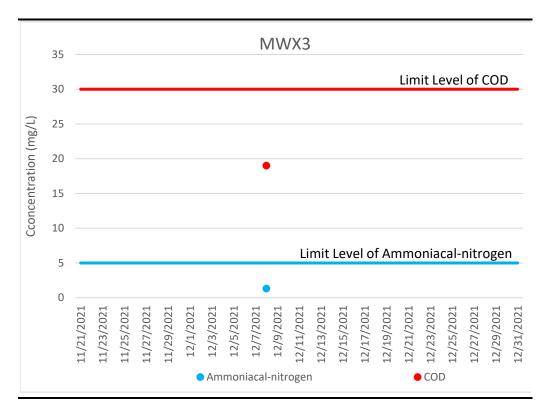


Figure F5.4 Graphical Presentation for Groundwater Monitoring (MWX-4)

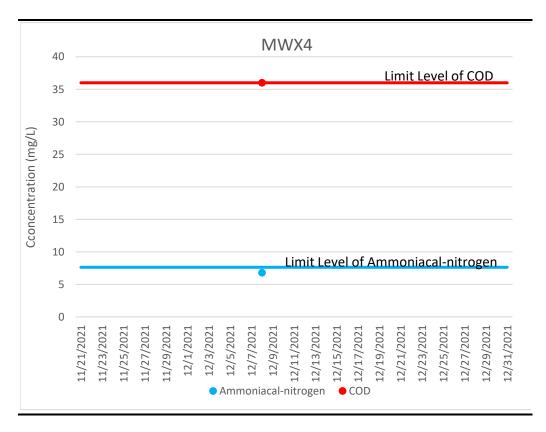


Figure F5.5 Graphical Presentation for Groundwater Monitoring (MWX-5)

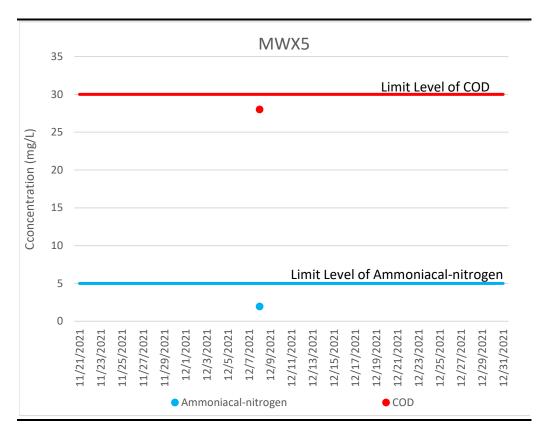


Figure F5.6 Graphical Presentation for Groundwater Monitoring (MWX-6)

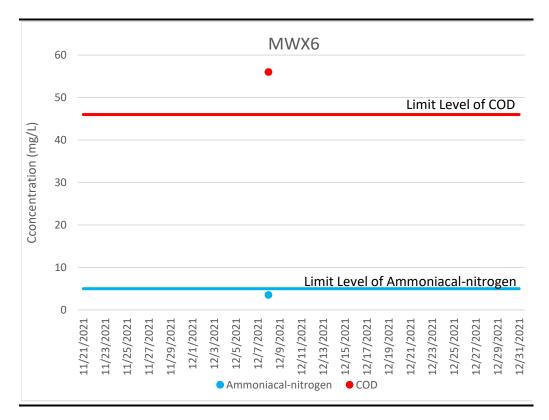


Figure F5.7 Graphical Presentation for Groundwater Monitoring (MWX-7)

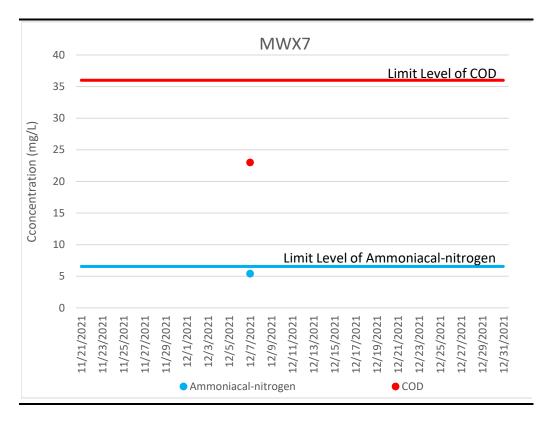


Figure F5.8 Graphical Presentation for Groundwater Monitoring (MWX-8)

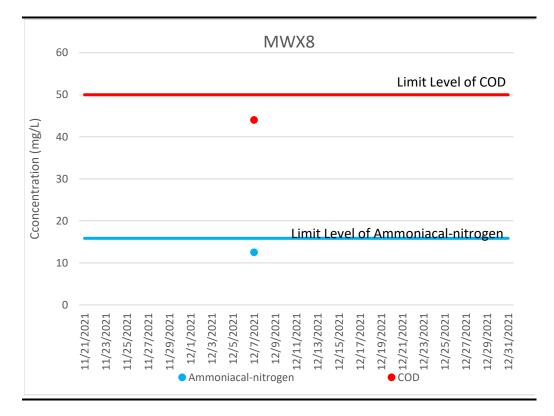


Figure F5.9 Graphical Presentation for Groundwater Monitoring (MWX-9)

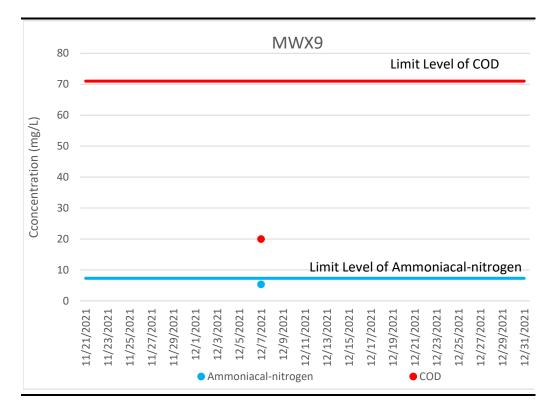


Figure F5.10 Graphical Presentation for Groundwater Monitoring (MWX-10)

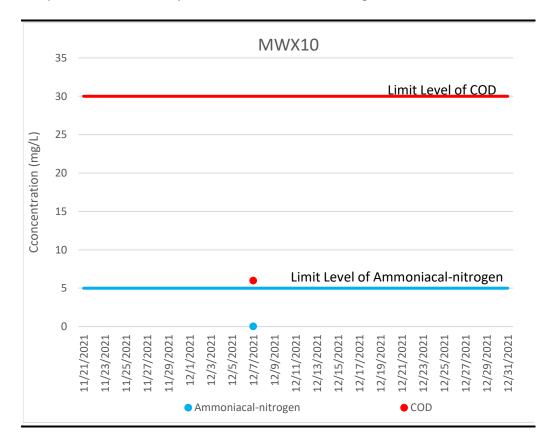


Figure F5.11 Graphical Presentation for Groundwater Monitoring (MWX-11)

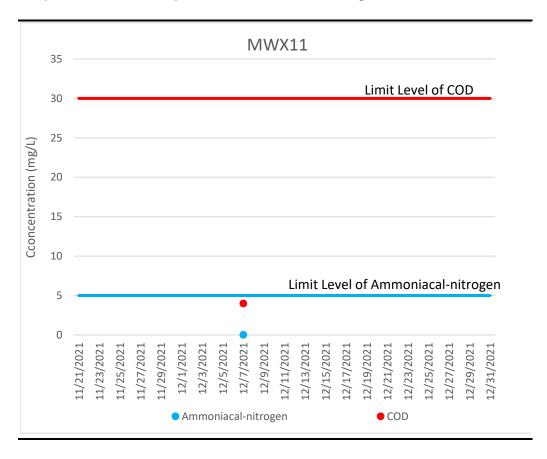


Figure F5.12 Graphical Presentation for Groundwater Monitoring (MWX-12)

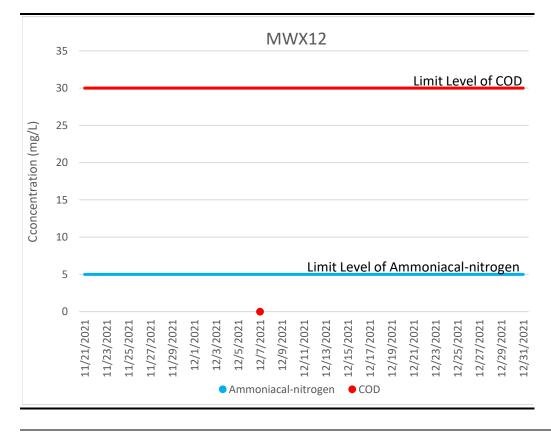


Figure F5.13 Graphical Presentation for Groundwater Monitoring (MWX-13)


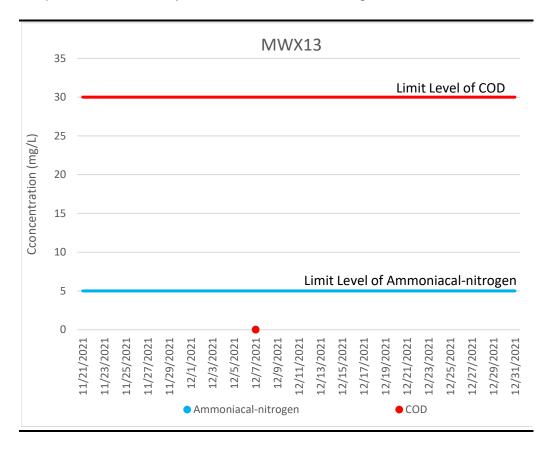


Figure F5.14 Graphical Presentation for Groundwater Monitoring (MWX-14)

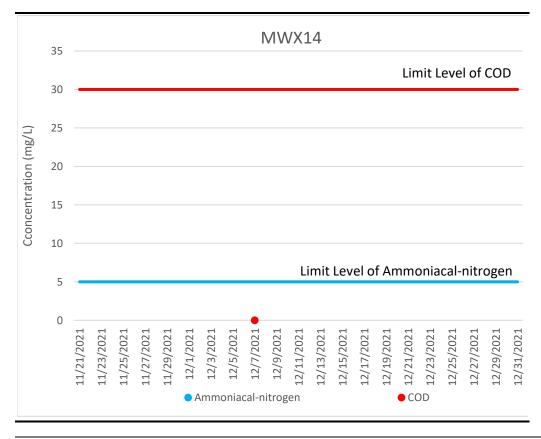

Annex F6

Investigation Reports of Environmental Quality Limit Exceedance


Project	South East New Territories (SENT) Landfill Extension
Date	8 December 2021
Time	10:15
Monitoring Location	MWX-6
Parameter	Chemical Oxygen Demand (COD)
Action / Limit Levels	>46 mg /L
Measured Level	56 mg /L
Possible reason	<ul> <li>Joing /L</li> <li>Groundwater contaminated with leachate is commonly characterized by high COD and ammoniacal-nitrogen levels as a result of degradation of organic matters in the waste. The groundwater quality (ammoniacal-nitrogen) monitoring results at MWX-6 (3.52mg/L) and groundwater quality (COD) monitoring results of the groundwater monitoring wells adjacent to MWX-6 (MWX-5: 28 mg/L and MWX-7: 23 mg/L) are well within the respective limit levels. In addition, no exceedance of COD Limit Levels for groundwater monitoring at other monitoring wells was recorded in the sampling event. Hence, there is a low possibility of the slight elevation of COD level at MWX-6 is due to leachate contamination from SENTX operation or at least it is not conclusive to base on this result to demonstrate exceedance is due to leachate contamination.</li> <li>In accordance with Table 4.5b of the updated EM&amp;A Manual, repeat measurement was conducted on 4 January 2022 to confirm findings. COD concentration of 44 mg/L (below Limit Level) was measured during the sampling event, which demonstrates no consecutive groundwater quality impact at MWX-6.</li> <li>In addition, in accordance with the findings of the desktop review commissioned by GVL and EPD (the Employer) in May 2021 to investigate the potential sources of the elevated methane levels at the perimeter landfill gas monitoring wells at SENTX, pockets of organic matters are identified in the fill materials of the SENTX site upon review of the historical site investigation borehole logs at the Project Site area. It is possible that the elevated COD concentration measured at MWX-6 (in close proximity to LFG13, which shows elevated methane levels continuous) on 8 December 2021could be due to localised organic matters within or around the monitoring</li> </ul>
	well. Due to the presence of influencing factor from non-project source; the COD levels at all other groundwater monitoring wells are within the respective limit level, and the subsequent month monitoring results at MWX-6 did not show exceedance, there is no adequate evidence showing that the COD level exceedance measured at MWX-6 on 8 December 2021 was deemed to Project-

### Investigation Report of Environmental Quality Limit Exceedance

	related activities.
Action Taken / Action to be Taken	Examination of environmental performance of the Project will be continued during the weekly inspections. The Contractor is reminded to implement relevant and appropriate mitigation measures according to the updated EM&A Manual to avoid any exceedance of the Action and Limit Levels.
Remarks	-
Prepared by: Abbey Lau	
Designation: Environmenta	l Team
Date: 26 January 202	22

### Landfill Gas

Landfill Gas Monitoring Locations for Service Voids, Utilities and Manholes along the Site Boundary and Within the SENTX Site

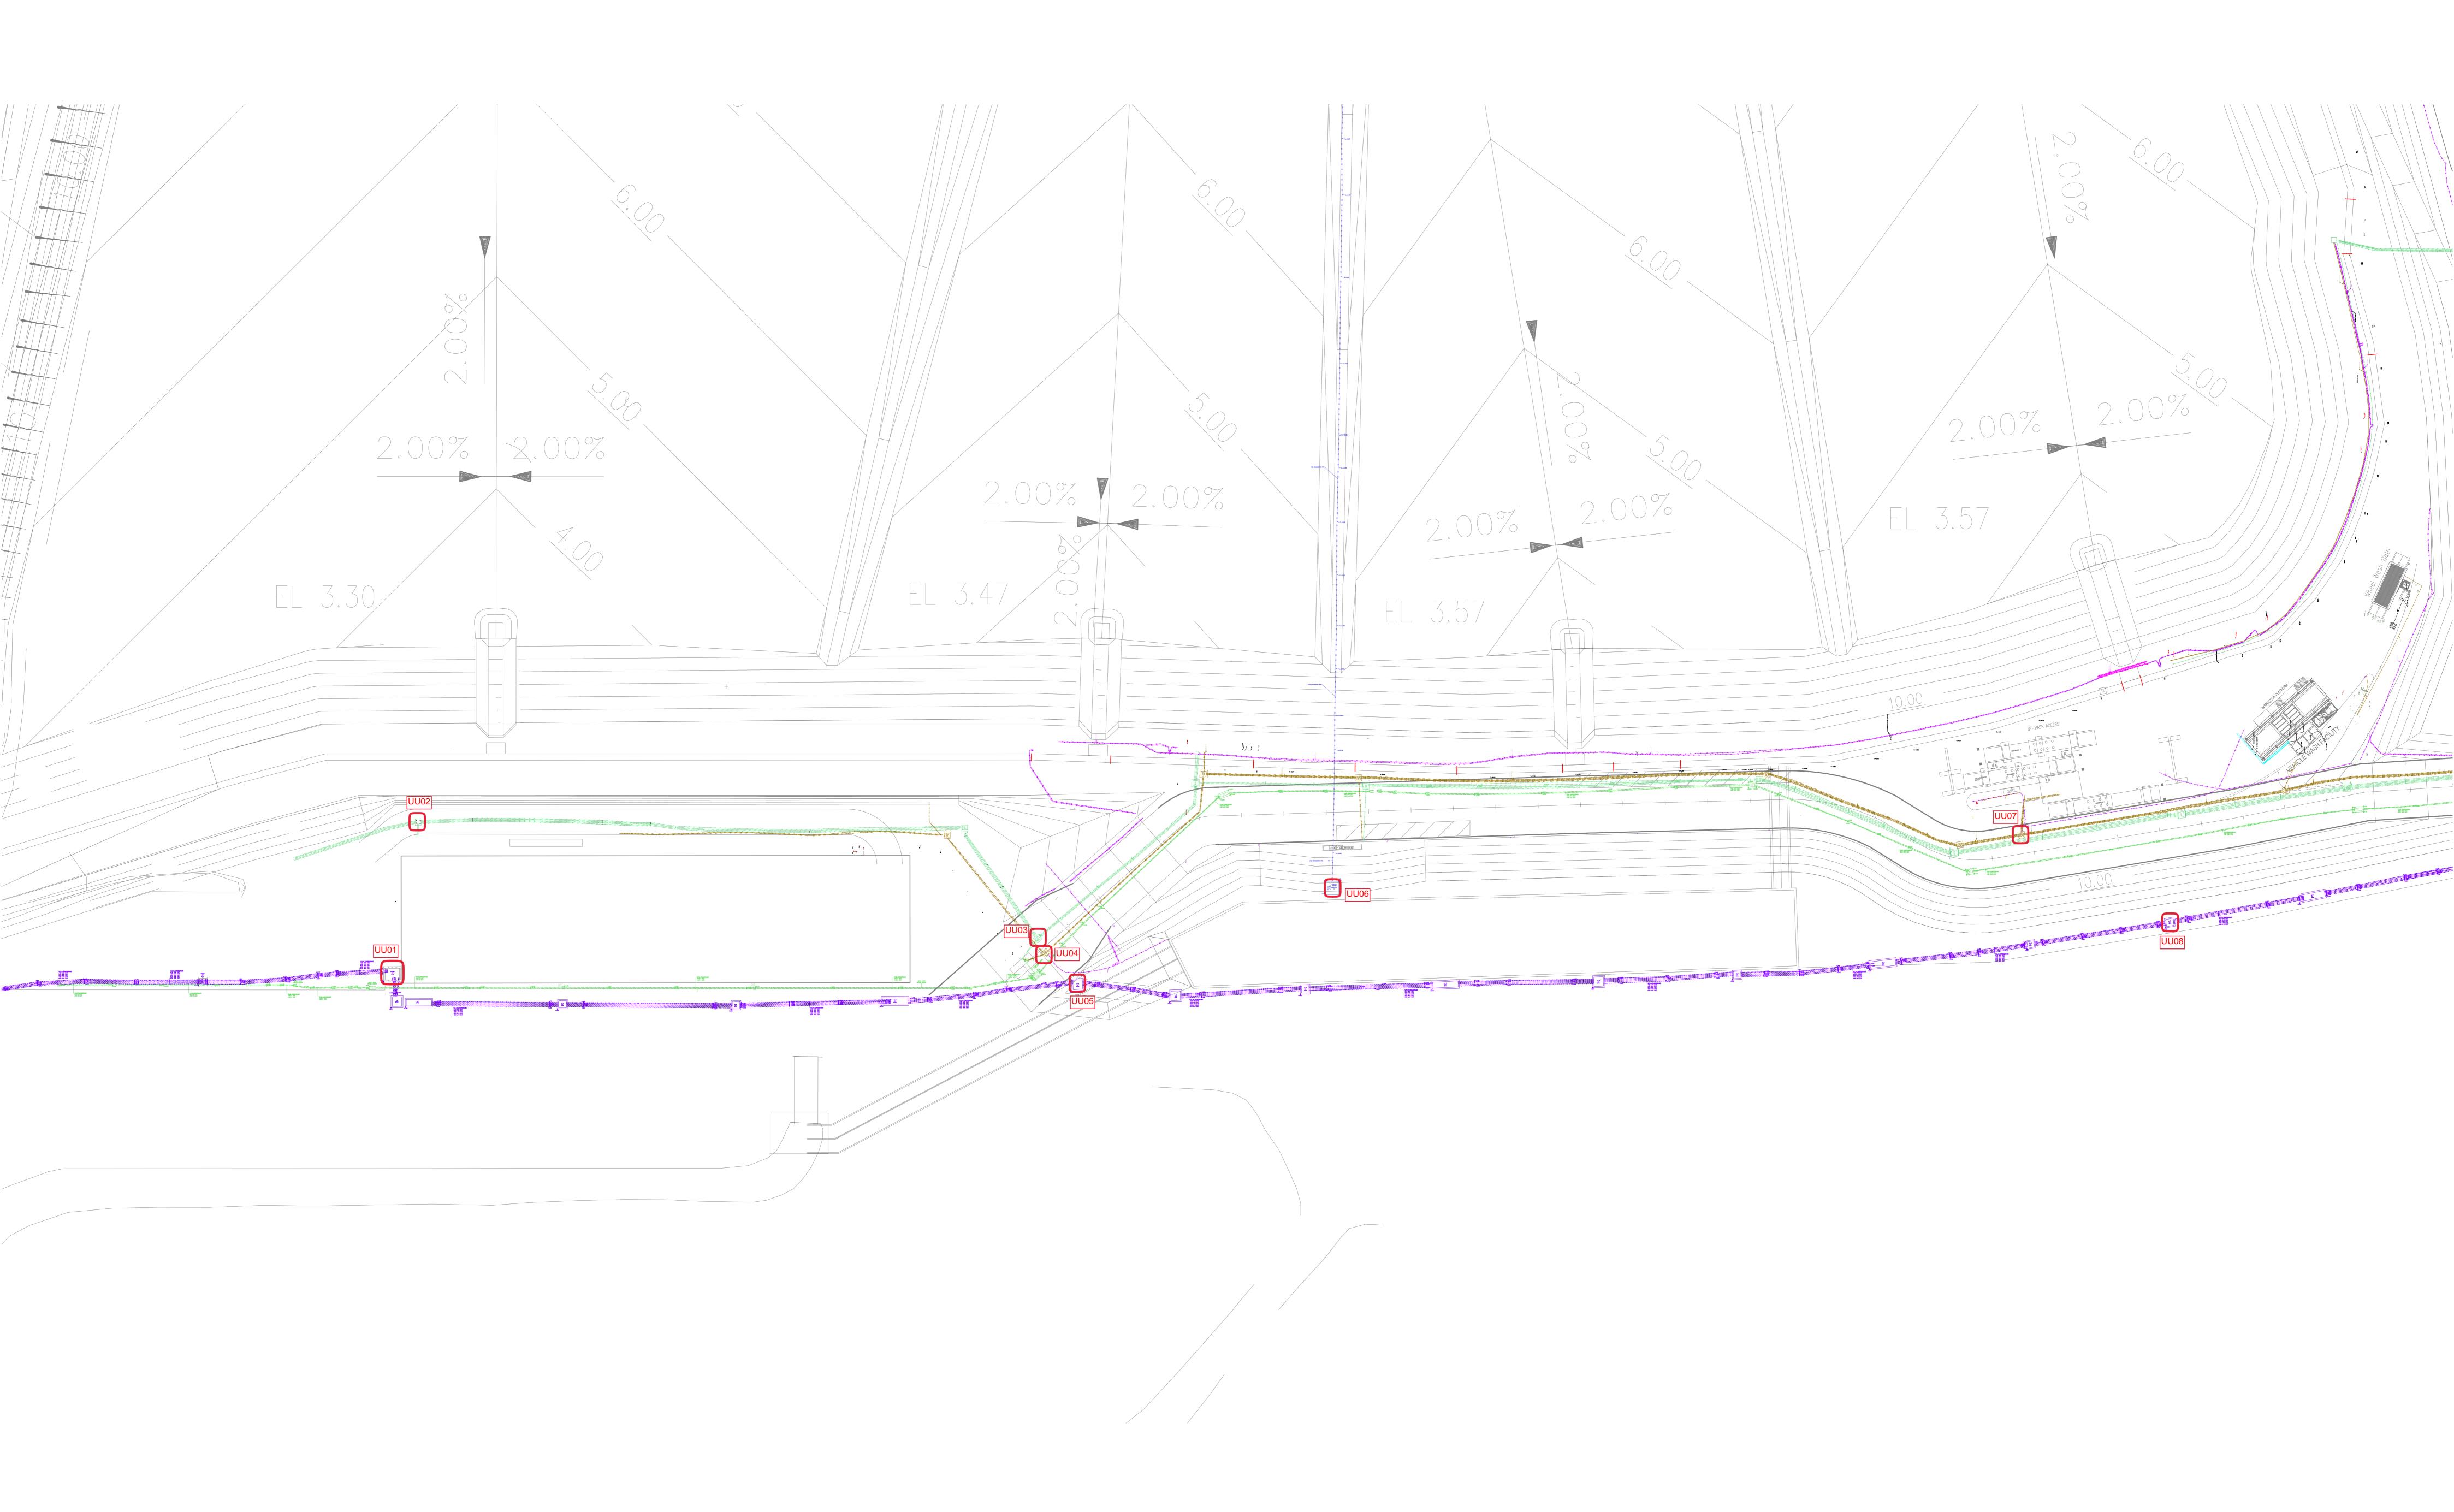



### Landfill Gas Monitoring Results

Location	Water Level (mPD)	Methane (% (v/v))	Carbon Dioxide (% (v/v))	Oxygen (% (v/v))
LFG1	2.40	0.0	0.1	18.9
LFG2	2.30	0.0	0.1	19.9
LFG3	2.33	0.0	0.9	17.4
LFG4	2.32	0.0	0.0	20.1
LFG5	2.65	0.0	0.2	7.2
LFG6	2.29	0.0	0.1	19.3
LFG7	2.48	0.0	0.0	17.6
LFG8	2.42	0.0	0.0	19.3
LFG9	2.38	0.0	0.1	8.8
LFG10	2.12	0.0	0.0	18.0
LFG11	2.29	0.0	0.1	7.8
LFG12	2.23	0.0	0.0	19.6
LFG13	2.07	19.6	0.0	0.4
LFG14	1.81	0.0	0.0	16.2
LFG15	2.05	1.8	0.4	12.7
LFG16	2.19	0.0	0.1	18.6
LFG17	2.38	0.0	0.2	0.8
LFG18	2.59	0.0	0.1	19.3
LFG19	2.74	0.0	0.1	3.6
LFG20	2.80	0.0	1.1	17.0
LFG21	2.85	0.0	2.0	9.7
LFG22	2.62	0.0	1.0	16.3
LFG23	12.52	0.0	2.1	18.1
LFG24	6.33	0.0	0.9	19.0
GP1	Probe bent	0.2	5.2	14.6
GP2 (shallow)	Probe bent	0.5	0.3	19.2
GP2 (deep)	Probe bent	0.2	0.1	19.6
GP3 (shallow)	Probe bent	0.3	2.5	14.4
GP3 (deep)	Probe bent	0.1	0.2	19.3
GP4 (shallow)	Probe bent	0.6	0.7	19.0
GP4 (deep)	Probe bent	0.7	1.7	17.4
GP5 (shallow)	Probe bent	0.1	5.4	16.8
GP5 (deep)	38.80	0.1	0.3	19.5
GP6	37.19	0.0	5.6	14.4
GP7	36.21	0.0	0.1	20.0
GP12	1.83	0.0	0.0	20.1
GP15	2.34	0.0	0.0	20.0
P7	2.32	0.0	0.0	20.0
P8	2.44	0.0	0.0	20.1
Р9	2.26	0.0	0.0	20.1

### Table G2.1Landfill Gas Monitoring Results at Perimeter LFG Monitoring Wells

Location	Methane (% (v/v))	Carbon Dioxide (% (v/v))	Oxygen (% (v/v))	
UU01	0.1	0.0	20.7	
UU02	0.0	0.0	20.7	
UU03	0.0	0.0	20.5	
UU04	0.1	0.0	20.6	
UU05	0.0	0.0	20.6	
UU06	0.0	0.0	20.5	
UU07	0.1	0.0	20.4	
UU08	0.0	0.0	20.5	
UU09	0.2	0.0	20.1	
UU10	0.1	0.0	20.3	
UU11	Inaccessible due to on-going construction work			
UU12	Inaccessible due to on-going construction work			
UU13	Inaccessible due to on-going construction work			
UU14	Inaccess	ible due to on-going const	ruction work	
UU15	0.1	0.0	20.2	
UU16	0.1	0.0	20.3	
UU17	0.3	0.0	20.3	
UU18	0.1	0.0	20.3	
UU19	0.0	0.0	20.7	
UU20	0.1	0.0	20.3	
UU21	0.0	0.0	19.4	
UU22	0.0	0.0	19.3	
UU23	0.0	0.0	19.3	
UU24	0.0	0.0	19.3	
UU25	0.0	0.0	19.2	
UU26	0.0	0.0	20.1	
UU27	0.0	0.0	19.5	
UU28	0.0	0.0	19.8	

## Event and Action Plan for Landfill Gas Monitoring

Event	Action				
	ET	IEC	Contractor		
Limit Level being exceeded for field monitoring at the perimeter monitoring wells	<ul> <li>Investigate the cause(s) of exceedance</li> <li>Prepare the Notification of Exceedance within 24 hours</li> <li>Check monitoring data, all plant, equipment and the Contractor's working methods</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Increase the monitoring frequency to daily if exceedance is due to the Project for monitoring wells in the areas where there is development within 250m of the SENTX Site Boundary and to weekly for other monitoring wells, until no exceedance of limit level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Repeat field measurement to confirm findings</li> <li>Check the performance of landfill gas management system</li> <li>Rectify unacceptable practice</li> <li>Discuss with the ET and IEC and submi proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate</li> </ul>		
Limit Level being exceeded for the bulk gas sampling at the perimeter monitoring wells	<ul> <li>Check and compare the results of field monitoring and laboratory analyse of bulk samples</li> <li>If the results of field monitoring also show exceedance, the action(s) for limit level being exceeded for field monitoring would have been triggered</li> <li>If the results of field monitoring does not show exceedance, the sampling procedures should be checked and if deems necessary, to repeat the monitoring and recalibrate the portable monitoring instruments</li> <li>Notify the above findings to Contractor and IEC</li> </ul>		• Nil		

#### Annex G3 Event and Action Plan for Landfill Gas Monitoring

Event		Action	
	ET	IEC	Contractor
Limit Level being exceeded at the permanent gas monitoring system	<ul> <li>Investigate the cause(s) of exceedance</li> <li>Prepare the Notification of Exceedance within 24 hours</li> <li>Check the methane gas level at the perimeter monitoring wells, manholes or utilities duct</li> <li>Check monitoring data, all plant, equipment and the Contractor's working methods</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Evacuate all staff in the concerned building</li> <li>Open the doors and window of all rooms on the ground floor</li> <li>Do not allow staff to go back to the room if methane level is higher than 1% gas</li> <li>Check the performance of the landfill gas management system</li> <li>Rectify unacceptable practice</li> <li>Consider changes of working methods</li> <li>Discuss with the ET and IEC and submit proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate</li> </ul>
Limit Level being exceeded during surface emission monitoring	<ul> <li>Repeat the measurement to confirm findings</li> <li>Investigate the cause(s) of exceedance</li> <li>Prepare the Notification of Exceedance within 24 hours</li> <li>Check monitoring data, all plant, equipment and the Contractor's working methods</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Increase the monitoring frequency to monthly if exceedance is due to the Project until no exceedance of limit level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>Audit the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Check landfill gas management system</li> <li>Rectify unacceptable practice</li> <li>Consider changes of working methods</li> <li>Discuss with the ET and IEC and submit proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate</li> </ul>

Event		Action				
	ET	IEC	Contractor			
Limit Level being exceeded at the service voids, utilities pits, manholes and location of vegetation stress	<ul> <li>Repeat the measurement to confirm findings</li> <li>Investigate the cause(s) of exceedance</li> <li>Prepare the Notification of Exceedance within 24 hours</li> <li>Check monitoring data, all plant, equipment and the Contractor's working methods</li> <li>Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project</li> <li>Discuss with Contractor and IEC for remedial measures required</li> <li>Ensure remedial measures are properly implemented</li> <li>Increase the monitoring frequency to weekly if exceedance is due to the Project until no exceedance of limit level</li> </ul>	<ul> <li>Verify the Notification of Exceedance</li> <li>Discuss with ET and Contractor on proposed remedial measures</li> <li>Review proposals on remedial measures</li> <li>Audit the implementation of the remedial measures</li> <li>the effectiveness of the implemented remedial measures</li> </ul>	<ul> <li>Check landfill gas management system</li> <li>Rectify unacceptable practice</li> <li>Discuss with the ET and IEC and submit proposals for remedial measures to IEC</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate</li> </ul>			

Annex H

Cumulative Statistics on Exceedances, Environmental Complaints, Notification of Summons and Status of Prosecutions

		Total No. recorded in this reporting period	Total No. recorded since project
			commencement
Air Quality (Dust)	Action	0	0
	Limit	1	1
Air Quality (Odour)	Action	0	0
	Limit	0	0
Air Quality (Emissions of Thermal	Limit	0	0
Oxidiser)			
Air Quality (Emissions of Landfill	Limit	1	1
Gas Flare)			
Air Quality (Emissions of Landfill	Limit	0	0
Gas Generator)			
Noise	Action	0	0
	Limit	0	0
Water Quality (Surface Water)	Limit	0	57
Water Quality (Leachate)	Limit	0	0
Water Quality (Groundwater)	Limit	1	1
Landfill Gas (Perimeter Landfill Gas	Limit	0	0
Monitoring Wells)			
Landfill Gas (Service Void, Utilities	Limit	0	0
and Manholes)			
Landfill Gas (Permanent Gas	Limit	0	0
Monitoring System)			

#### Table H1Cumulative Statistics on Exceedances

# Table H2Cumulative Statistics on Complaints, Notifications of Summons and Successful<br/>Prosecutions

<b>Reporting Period</b>	Cumulative Statistics		
	Complaints	Notifications of Summons	Prosecutions
This Reporting Period (1 Oct 2021 – 31 Dec 2021)	0	0	0
Total no. received since project commencement	1	0	0
