



South East New Territories (SENT) Landfill Extension

Monthly Environmental Monitoring & Audit Report No.43 for July 2022

September 2022

ERM

2509, 25/F One Harbourfront 18 Tak Fung Street Hunghom, Kowloon Hong Kong T: 2271 3000 F: 3015 8052 www.erm.com





South East New Territories (SENT) Landfill Extension

Environmental Certification Sheet EP-308/2008/B and FEP-01/308/2008/B

Reference Document/Plan

Document/Plan to be Certified/Verified:

Monthly Environmental Monitoring & Audit Report No.43 for July 2022 for South East New Territories (SENT) Landfill

Extension

Date of Report:

13 September 2022

Reference EP Condition

EP Condition:

Condition No. 3.4

Four hard copies and one electronic copy of monthly EM&A Report shall be submitted to the Director within 10 working days after the end of the reporting month. The EM&A Reports shall include a summary of all non-compliance (exceedances) of the environmental quality performance limits (Action and Limit Levels). The submissions shall be verified by the IEC. Additional copies of the submission shall be provided to the Director upon request by the Director.

ET Certification

I hereby certify that the above referenced document/plan complies with the above referenced condition of EP-308/2008/B and FEP-01/308/2008/B.

Wardwitt J.

Frank Wan,

Environmental Team Leader:

(ERM Hong-Kong, Limited)

Date:

13 September 2022

IEC Verification

I hereby verify that the above referenced document/plan complies with the above referenced condition of EP-308/2008/B and FEP-01/308/2008/B.

Claudine Lee,

Independent Environmental Checker:

(Meinhardt Infrastructure and

Environment Limited)

Date: 14 September 2022

South East New Territories (SENT) Landfill Extension

Monthly Environmental Monitoring & Audit Report for July 2022

Environmental Resources Management

2509, 25/F, One Harbourfront 18 Tak Fung Street Hunghom, Kowloon Hong Kong

Telephone: (852) 2271 3000 Facsimile: (852) 3015 8052 E-mail: post.hk@erm.com http://www.erm.com

Client:		Projec	ct No:			
Green Valley Landfill Ltd.			0465169			
Summary		Date:				
		13 September 2022				
		Appro	ved by:			
This document presents the Monthly EM&A Report No.43 for July 2022 for South East New Territories (SENT) Landfill Extension		Warditt J.				
		Frank Wan Partner				
1	Monthly EM&A Report No.43 (for July 2022) (ES, S2.1.1, S2.3.2, S2.9, Annex D8, Annex F6 revised)	AL	FW	FW	13 Sep 2022	
0	Monthly EM&A Report No.43 (for July 2022)	AL	FW	FW	9 Aug 2022	
Revision	Description	Ву	Checked	Approved	Date	
		Distrib	oution			
This report has been prepared by Environmental Resources Management the trading name of 'ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business			Internal			
and taking account of the resources devoted to it by agreement with the client.		\boxtimes	Public			
We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.			Confide	ntial		
This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies on the report at their own risk.		bsi) 9001 Outers Management)	150 45001 temporalist Heats and Salety Management		



CONTENTS

	EXECUTIVE SUMMARY	1
1	INTRODUCTION	1
1.1	BACKGROUND	1
1.2	PROJECT DESCRIPTION	1
1.3	SCOPE OF THE EM&A REPORT	2
1.4	PROJECT ORGANISATION	2
1.5	SUMMARY OF CONSTRUCTION WORKS	3
1.6	SUMMARY OF EM&A PROGRAMME REQUIREMENTS	4
1.7	STATUS OF STATUTORY ENVIRONMENTAL COMPLIANCE WITH THE	
	ENVIRONMENTAL PERMIT	5
1.8	STATUS OF OTHER STATUTORY ENVIRONMENTAL REQUIREMENTS	5
2	EM&A RESULTS	7
2.1	AIR QUALITY MONITORING	7
2.2	NOISE MONITORING	16
2.3	Water Quality Monitoring	18
2.4	LANDFILL GAS MONITORING	27
2.5	LANDSCAPE AND VISUAL MONITORING	31
2.6	EM&A SITE INSPECTION	32
2.7	WASTE MANAGEMENT STATUS	34
2.8	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	34
2.9	SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMA	NCE
	LIMIT	34
2.10	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL	
	PROSECUTIONS	35
3	FUTURE KEY ISSUES	36
3.1	CONSTRUCTION PROGRAMME FOR THE COMING MONTH	36
3.2	KEY ISSUES FOR THE COMING MONTH	36
3.3	MONITORING SCHEDULE FOR THE COMING MONTH	36
4	CONCLUSION AND RECOMMENDATION	37

ANNEXES

ANNEX A WO	ORK PROGRAMME

ANNEX B ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE

ANNEX C MONITORING SCHEDULE FOR THIS REPORTING PERIOD

ANNEX D AIR QUALITY

ANNEX D1 CALIBRATION CERTIFICATES FOR DUST MONITORING EQUIPMENT

ANNEX D2 24-HOUR TSP MONITORING RESULTS

ANNEX D3 EVENT AND ACTION PLAN FOR AIR QUALITY MONITORING

ANNEX D4 METEOROLOGICAL DATA

ANNEX D5 CERTIFICATES OF THE QUALIFIED ODOUR PANELIST

ANNEX D6 ODOUR MONITORING RESULTS

ANNEX D7 THERMAL OXIDIZER, LANDFILL GAS FLARE AND LANDFILL GAS

GENERATOR STACK EMISSION MONITORING RESULTS

ANNEX D8 INVESTIGATION REPORTS OF ENVIRONMENTAL QUALITY LIMIT EXCEEDANCE

ANNEX E NOISE

ANNEX E1 CALIBRATION CERTIFICATES FOR NOISE MONITORING EQUIPMENT

ANNEX E2 NOISE MONITORING RESULTS

ANNEX E3 EVENT AND ACTION PLAN FOR NOISE MONITORING

ANNEX F WATER QUALITY

ANNEX F1 CALIBRATION CERTIFICATES FOR SURFACE WATER QUALITY MONITORING EQUIPMENT

ANNEX F2 SURFACE WATER QUALITY MONITORING RESULTS

ANNEX F3 EVENT AND ACTION PLAN FOR WATER QUALITY MONITORING

ANNEX F4 CALIBRATION CERTIFICATES FOR EFFLUENT QUALITY MONITORING EQUIPMENT

ANNEX F5 LEACHATE LEVELS MONITORING RESULTS

ANNEX F6 EFFLUENT QUALITY MONITORING RESULTS

ANNEX F7 CALIBRATION CERTIFICATES FOR GROUNDWATER MONITORING EQUIPMENT

ANNEX F8 GROUNDWATER MONITORING RESULTS

ANNEX F9 INVESTIGATION REPORTS OF ENVIRONMENTAL QUALITY LIMIT EXCEEDANCE

ANNEX G LANDFILL GAS

ANNEX G1 LANDFILL GAS MONITORING LOCATIONS FOR SERVICE VOIDS, UTILITIES AND MANHOLES ALONG THE SITE BOUNDARY AND WITHIN THE SENTX SITE

ANNEX G2 CALIBRATION CERTIFICATES FOR LANDFILL GAS MONITORING EQUIPMENT

ANNEX G3 LANDFILL GAS MONITORING RESULTS

ANNEX G4 EVENT AND ACTION PLAN FOR LANDFILL GAS MONITORING

ANNEX H CUMULATIVE STATISTICS ON EXCEEDANCES, ENVIRONMENTAL COMPLAINTS, NOTIFICATION OF SUMMONS AND STATUS OF PROSECUTIONS

ANNEX I MONITORING SCHEDULE FOR THE NEXT REPORTING PERIOD

EXECUTIVE SUMMARY

The SENT Landfill Extension (SENTX) forms an integral part in the Strategic Plan in maintaining the continuity of landfill capacity in the Hong Kong for the cost-effective and environmentally satisfactory disposal of waste. ERM-Hong Kong, Limited (ERM) is commissioned to undertake the role of Environmental Team (ET) for the construction, operation/restoration and aftercare of SENTX Project ("the Project") in accordance with the requirements specified in the Environmental Permit (EP), updated Environmental Monitoring and Audit (EM&A) Manual, the approved Environmental Impact Assessment (EIA) Report of the Project taking account of the latest design and other relevant statutory requirements. The construction (not including works related to site clearance and preparation) and operation of the Project commenced on 2 January 2019 and 21 November 2021, respectively.

This Monthly EM&A report presents the EM&A works carried out during the period from 1 to 31 July 2022 for the Project in accordance with the updated EM&A Manual.

Exceedance of Action and Limit Levels for Air Quality

Two exceedances of Action and Limit Levels for Total Suspended Particulates (TSP) were recorded for air quality monitoring in the reporting period. The TSP exceedance at AM2 was considered Project-related while the exceedance at AM4 on 29 July 2022 was considered non-Project-related upon further investigation.

Exceedance of Action and Limit Levels for Noise

No exceedance of Action and Limit Levels for operation/ restoration phase noise monitoring was recorded in the reporting period.

Exceedance of Action and Limit Levels for Water Quality

One exceedance of the Limit Level for suspended solid (SS) was recorded for additional surface water quality monitoring at DP4 in the reporting period. The SS exceedance at DP4 on 8 July 2022 was considered project-related upon further investigation. The surface water monitoring results (SS) at DP4 on 15 July 2022 complied with the Limit Level as stipulated in the updated EM&A Manual and the weekly surface water monitoring (SS) at DP4 was terminated.

Exceedance of Action and Limit Levels for Landfill Gas

No exceedance of Action and Limit Levels for operation/ restoration phase landfill gas monitoring was recorded in the reporting period.

Environmental Complaints, Summons and Prosecutions

There were no complaints, notification of summons or prosecution recorded in the reporting period.

Reporting Change

There was no reporting change in the reporting period.

Future Key Issues

Potential environmental impacts arising from the upcoming construction/ operational activities in the next reporting period of August 2022 are mainly associated with potential surface water impact in the rainy season.

1 INTRODUCTION

1.1 BACKGROUND

The SENT Landfill Extension (SENTX) forms an integral part in the Strategic Plan in maintaining the continuity of landfill capacity in the Hong Kong for the cost-effective and environmentally satisfactory disposal of waste. The *Environmental Impact Assessment (EIA) Report* and the associated *Environmental Monitoring and Audit (EM&A) Manual* for the construction, operation, restoration and aftercare of the SENTX (hereafter referred to as "the Project") have been approved under the *Environmental Impact Assessment Ordinance (EIAO)* in May 2008 (Register No.: AEIAR-117/2008) (hereafter referred to as the approved EIA Report) and an Environmental Permit (EP-308/2008) (EP) was granted by the Director of Environmental Protection (DEP) on 5 August 2008.

Since then, applications for Variation of an Environmental Permit (No. VEP-531/2017) were submitted to EPD and the Variation of Environmental Permits (EP-308/2008/A and EP-308/2008/B) were granted on 6 January 2012 and 20 January 2017, respectively, as the Hong Kong SAR Government has decided to reduce the scale of the design scheme of SENTX assessed in the approved EIA Report and SENTX will only receive construction waste. In May 2018, a Further Environmental Permit (FEP) (FEP-01/308/2008/B) was granted to the SENTX's contractor, Green Valley Landfill, Limited (GVL).


ERM-Hong Kong, Limited (ERM) and Meinhardt Infrastructure and Environment Limited (Meinhardt) are commissioned to undertake the roles of Environmental Team (ET) and the Independent Environmental Checker (IEC), respectively, to undertake the EM&A activities for the Project in accordance with the requirements specified in the EP, updated EM&A Manual (1), approved EIA Report (2) taking account of the latest design and other relevant statutory requirements.

1.2 PROJECT DESCRIPTION

The SENTX is a piggyback landfill, occupying the southern part of the existing SENT Landfill (including its infrastructure area) and 13 ha of Tseung Kwan O (TKO) Area 137. A layout plan of the SENTX is shown in *Figure 1.1*. Under the latest design, the SENTX has a net void capacity of about 6.5 Mm³ and provides an additional lifespan of about 6 years, commencing operation upon exhaustion of the SENT Landfill. The SENTX will receive construction waste only.

⁽¹⁾ ERM (2018). South East New Territories (SENT) Landfill Extension: Environmental Monitoring & Audit Manual

⁽²⁾ ERM (2007). South East New Territories (SENT) Landfill Extension - Feasibility Study: Environmental Impact Assessment Report

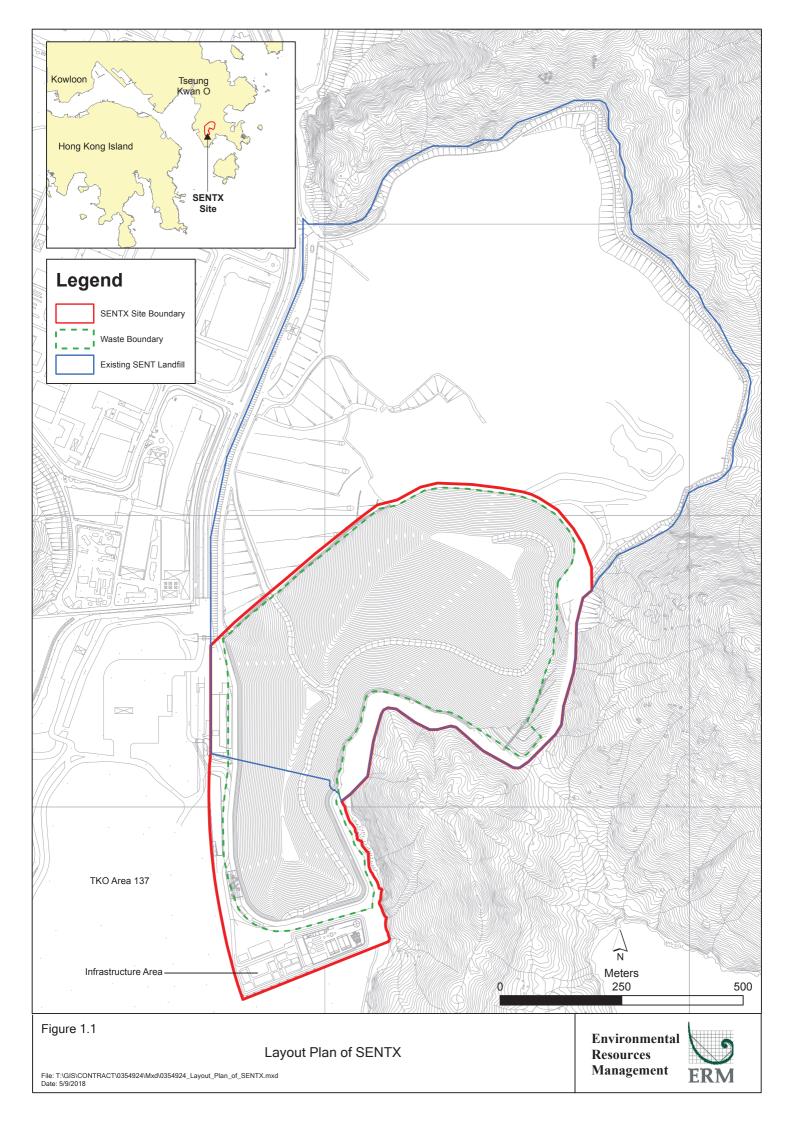

The key implementation milestones of the Project are indicatively summarised in *Table 1.1*. The construction works and operation of the Project commenced on 2 January 2019 and 21 November 2021, respectively.

 Table 1.1
 Estimated Key Dates of Implementation Programme

Key Stage of the Project	Indicative Date
Start construction	2 January 2019
Commissioning of new infrastructure facilities	2020
Demolition of existing infrastructure facilities	2021
Start waste intake at SENTX	21 November 2021
Estimated exhaustion date of SENTX	2027
End of aftercare for SENTX	2057

The major construction works of the SENTX includes:

- Site formation at the TKO Area 137 and the existing infrastructure area at SENT Landfill;
- Construction of surface and groundwater drainage systems;
- Construction of the leachate containment and collection systems;
- Construction of new leachate and landfill gas treatment facilities, site offices, maintenance yards at the new infrastructure area;
- Construction of new pipelines to transfer the leachate and landfill gas
 collected from the existing SENT Landfill to the treatment facilities at the
 new infrastructure area;
- Construction of the site access and new waste reception facilities; and
- Demolition of the facilities at the existing SENT Landfill infrastructure area.


1.3 SCOPE OF THE EM&A REPORT

This is the Monthly EM&A Report for the Project which summarises the key findings of the EM&A programme during the reporting period from 1 to 31 July 2022 for the construction and operation works.

1.4 PROJECT ORGANISATION

The organisation structure of the Project is presented in *Figure 1.2*.

Figure 1.2 Organisation Chart

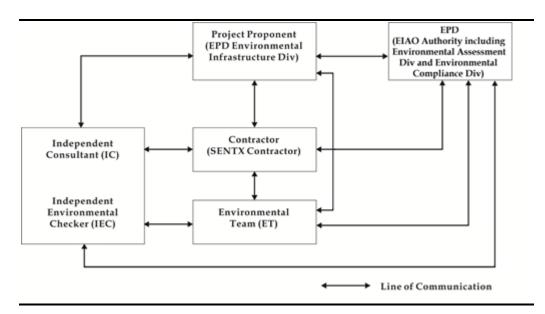

Contact details of the key personnel are summarised in *Table 1.2* below.

Table 1.2 Contact Information of Key Personnel

Party	Position	Name	Telephone
Contractor	Project Manager	Carl Lai	2706 8829
(Green Valley Landfill Limited)			
Environmental Team (ET) (ERM-Hong	ET Leader	Frank Wan	2271 3152
Kong, Limited)			
Independent Environmental Checker (IEC)	IEC	Claudine Lee	2859 5409
(Meinhardt Infrastructure and			
Environment Limited)			

1.5 SUMMARY OF CONSTRUCTION WORKS

The programme of the construction is shown in *Annex A*. As informed by the Contractor, the major works carried out in this reporting period include:

- Rectification of defects at Landfill Gas (LFG) Plant, Leachate Treatment Plant (LTP), infrastructure area and waste reception area;
- Landscaping works at infrastructure area;
- Rectification of defects for underground utilities and pipe;
- Construction of road pavement on top of the MSE wall;
- Construction of Cell 4X and SENT tie in area;
- Construction of perimeter channel X10A and X10C along Western bund of Cell 4X;

- Maintenance and improvement of temporary surface water drainage; and
- Rectification of utilities installation along Western bund of Cell 4X.

The implementation schedule of the mitigation measured recommended in the Updated EM&A Manual is presented in *Annex B*.

1.6 SUMMARY OF EM&A PROGRAMME REQUIREMENTS

The status for all environmental aspects are presented in *Table 1.3*. The EM&A requirements remained unchanged during the reporting period.

Table 1.3 Summary of Status for the Environmental Aspects under the Updated EM&A Manual

Parameters	Status
Air Quality	
Baseline Monitoring	The results of baseline air quality monitoring were reported in Baseline Monitoring Report and Pre-operation Baseline Monitoring Report and submitted to EPD under EP Condition 3.3
Impact Monitoring	On-going On-going
Noise	
Baseline Monitoring	The results of baseline noise monitoring were reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.3
Impact Monitoring	On-going On-going
Water Quality	
Baseline Monitoring	The results of baseline surface water quality monitoring were reported in Baseline Monitoring Report and Pre-operation Baseline Monitoring Report and submitted to EPD under EP Condition 3.3
Impact Monitoring	On-going On-going
Landfill Gas	
Impact Monitoring	On-going On-going
Waste Management	
Waste Monitoring	On-going On-going
Landscape and Visual	
Baseline Monitoring	The results of baseline landscape and visual monitoring were reported in Baseline Monitoring Report and submitted to EPD under EP Condition 3.3
Operation Phase Audit	On-going On-going
Site Environmental Audit	
Regular Site Inspection	On-going On-going
Complaint Hotline and Email	On-going
Environmental Log Book	On-going

Taking into account the operation works, impact monitoring of air quality, noise, water quality, landfill gas and waste management were carried out in the reporting period. The impact monitoring schedule of air quality, noise, water quality and landfill gas monitoring are provided in *Annex C*.

The EM&A programme also involved environmental site inspections and related auditing conducted by the ET for checking the implementation of the required environmental mitigation measures recommended in the approved EIA Report and relevant EP submissions. To promote the environmental awareness and enhance the environmental performance of the contractors, environmental trainings and regular environmental management meetings were conducted during the reporting period, which are summarised as below:

- One environmental management meeting was held with the Contractor, ER, ET, IEC and EPD on 21 July 2022; and
- Environmental toolbox trainings on Illegal Dumping and Air Pollution –
 Dark Smoke were provided on 6 July and 20 July 2022 respectively by the
 Contractor to the workers.

1.7 STATUS OF STATUTORY ENVIRONMENTAL COMPLIANCE WITH THE ENVIRONMENTAL PERMIT

The status of statutory environmental compliance with the EP conditions under the EIAO, submission status under the EP and implementation status of mitigation measures are presented in *Table 1.4*.

Table 1.4 Status of Submissions required under the EP and Implementation Status of Mitigation Measures

EP	Submission/Implementation Status	Status
Condition		
2.3	Management Organisation of Main	Submitted and accepted by EPD.
	Construction Companies	
2.4	Setting up of Community Liaison Group	Community Liaison Group was set up.
2.5	Submission of Detailed Landfill Gas	Submitted and accepted by EPD on 10
	Hazard Assessment Report	January 2019.
2.6	Submission of Restoration and Ecological	Submitted to EPD on 28 June 2019.
	Enhancement Plan	
2.7	Setting up of Trial Nursery	Trial Nursery works was commenced
		on 28 August 2019.
2.8	Advance Screen Planting	Advance Screen Planting works were
		completed on 28 June 2019.
2.9	Provision of Multi-layer Composite Liner	Under implementation.
	System	

1.8 STATUS OF OTHER STATUTORY ENVIRONMENTAL REQUIREMENTS

The environmental licenses and permits (including EP, *Water Pollution Control Ordinance* (WPCO) discharge license, registration as a chemical waste producer, and construction noise permit) that are valid in the reporting period are presented in *Table 1.5*. No non-compliance with environmental statutory requirements was identified.

Table 1.5 Status of Statutory Environmental Requirements

Description	Ref No.	Status
Environmental Permit	EP-308/2008	Granted on 5 August 2008
Variation of Environmental Permit	EP-308/2008/A	Granted on 6 January 2012
	EP-308/2008/B	Granted on 20 January 2017
Further Environmental Permit	FEP-01/308/2008/B	Granted on 16 May 2018
Water Discharge License under	Licence No.: WT00041447-	Validity from 17 June 2022
WPCO (Permit Holder: GVL)	2022	to 30 June 2024
Billing Account for Disposal of	Chit Account Number:	Approved on 28 December
Construction Waste	5001692	2005
Registration as a Chemical Waste	5296-839-G2228-01	Issued on 31 December 2015
Producer (Permit Holder: GVL)		
Construction Noise Permit (Permit	GW-RE0565-22	Validity from 15 June 2022
Holder: GVL)		to 14 December 2022
Construction Noise Permit (Permit	GW-RE0278-22	Validity from 31 March
Holder: Paul Y.)		2022 to 22 September 2022

2 EM&A RESULTS

The EM&A programme for the Project required environmental monitoring for air quality, noise, water quality and landfill gas as well as environmental site inspections for air quality, noise, water quality, landfill gas, waste management, and landscape and visual impacts. The EM&A requirements and related findings for each component are summarised in the following sections.

2.1 AIR QUALITY MONITORING

2.1.1 Dust Monitoring

Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, impact dust monitoring (in term of Total Suspended Particulates (TSP)) was carried out at the four designated locations along the site boundary (i.e. AM1, AM2, AM3 and AM4) during the operation/restoration phase, at a 6-day interval.

The Action and Limit Levels of the dust monitoring is provided in *Table 2.1* below.

Table 2.1 Action and Limit Levels for 24-hour TSP

Monitoring Station	Action Level	Limit Level
AM1 - SENTX Site Boundary (North)		_
AM2 - SENTX Site Boundary (West, near DP3)	260	2(0,, 3
AM3 - SENTX Site Boundary (West, near RC15)	260 μg m- ³	260 μg m- ³
AM4 - SENTX Site Boundary (West, near EPD building)		

High volume air samplers (HVSs) in compliance with the specifications listed under Section 3.2.2 of the updated EM&A Manual were used to measure 24-hour TSP levels at the dust monitoring stations. The HVSs were calibrated upon installation and thereafter at bi-monthly intervals to check the validity and accuracy of the results.

The equipment used in the impact dust monitoring programme and monitoring locations are summarised in *Table 2.2* and illustrated in *Figure 2.1*, respectively. Copies of the calibration certificates for the equipment are presented in *Annex D1*.

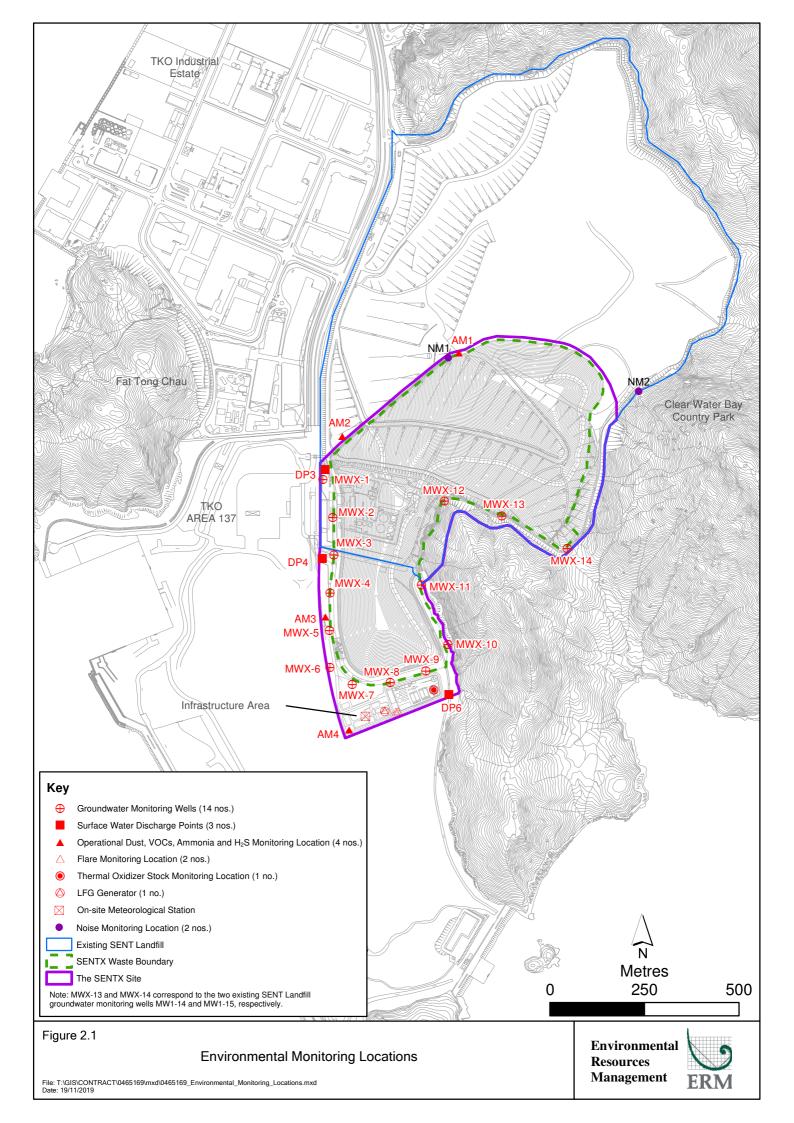


Table 2.2 Dust Monitoring Details

Monitoring Station	Location	Parameter	Frequency and Duration	U	Equipment
AM1	SENTX Site Boundary (North)	24-hour TSP	Once every 6 days	5, 11, 17, 23, 29 July 2022	Tisch TE-5170 (S/N: 1190)
AM2	SENTX Site Boundary (West, near DP3)				Tisch TE-5170 (S/N: 1047)
AM3	SENTX Site Boundary (West, near RC15)				Tisch TE-5170 (S/N: 1258)
AM4	SENTX Site Boundary (West, near EPD building)				Tisch TE-5170 (S/N: 1101)

Monitoring Schedule for the Reporting Month

The schedule for dust monitoring during the reporting period is provided in *Annex C*.

Results and Observations

The monitoring results for 24-hour TSP are summarised in *Table 2.3*. The detailed monitoring results and the graphical presentation of the 24-hour TSP results at each monitoring location are provided in *Annex D2*.

Table 2.3 Summary of 24-hour TSP Monitoring Results in the Reporting Period

Monitoring Station	Average 24-hr TSP Concentration (µg m ⁻³) (Range in bracket)	Action Level (μg/m³)	Limit Level (μg/m³)
AM1 - SENTX Site Boundary (North)	69 (39 – 156)	260	260
AM2 - SENTX Site Boundary (West, near DP3)	127 (43 – 312)	260	260
AM3 - SENTX Site Boundary (West, near RC15)	119 (56 – 241)	260	260
AM4 - SENTX Site Boundary (West, near EPD building)	144 (42 – 364)	260	260

The major dust sources in the reporting period included fugitive dust emission from exposed area in SENTX, as well as nearby operations of the SENTX and the TKO Area 137 Fill Bank.

Action and Limit Levels exceedances were recorded for TSP monitoring in the reporting period and actions in accordance with the Event and Action Plan presented in *Annex D3* were undertaken. Investigation of the Action and Limit Levels exceedances was conducted and the investigation report is presented in *Annex D8*.

Based on the investigation conducted for the monitoring event with potential Action and Limit Levels exceedance with the Contractor and the IEC, the TSP exceedance at AM2 was considered Project-related while the exceedance at AM4 on 29 July 2022 was considered non-Project-related. Repeat measurement had been scheduled on 4 August 2022 to confirm findings and no exceedance at AM2 and AM4 was recorded.

The Contractor was reminded to implement all relevant mitigation measures for the construction and operation works and maintain good site practice. The ET will keep track on the monitoring data and ensure Contractor's compliance of the environmental requirements.

Meteorological Data

Meteorological data obtained from the SENTX on-site meteorological monitoring station was used for the dust monitoring and is shown in *Annex D4*. It is considered that meteorological data obtained at the on-site meteorological monitoring station is representative of the Project area and could be used for the operation/restoration phase dust monitoring programme for the Project.

2.1.2 Odour Monitoring

Monitoring Requirements

According to the updated EM&A Manual of the Project, odour patrol was carried out along the site boundary during the operation/ restoration phase.

During the first month of operation, daily odour patrol (3 times per day) was conducted jointly by the ET and the IEC. The odour intensity detected was based on that determined by the IEC. In addition, an independent party (ALS Technichem (HK) Pty Ltd.) was appointed to undertake odour patrol together with the ET and IEC three times per week. During these patrols, the odour intensity detected was based on that determined by the independent third party.

Reduction of odour monitoring frequency from Period 1 (daily, three times per day) to Period 2 (weekly) was approved by EPD on 4 February 2022. Weekly odour patrol was conducted jointly by the ET and the IEC from 10 February 2022. In addition, an independent party (ALS Technichem (HK) Pty Ltd.) was appointed to undertake odour patrol together with the ET and IEC once every two weeks.

Reduction of odour monitoring frequency from Period 2 (weekly) to Period 3 (monthly) was approved by EPD on 2 June 2022. Monthly odour patrol was conducted jointly by the ET and the IEC from 28 June 2022. In addition, an independent party (ALS Technichem (HK) Pty Ltd.) was appointed to undertake odour patrol together with the ET and IEC quarterly.

The Action and Limit Levels for odour patrol is provided in *Table 2.4* below.

Table 2.4 Action and Limit Levels for Odour Patrol

Parameter	Action Level	Limit Level
Perceived odour intensity and odour complaints	 Odour intensity ≥ Class 2 recorded; or One documented complaint received 	 Odour intensity ≥ Class 3 recorded on 2 consecutive patrol ^(a) ^(b)

- (a) i.e. either Class 3-strong or Class 4-extreme odour intensity.
- (b) The exceedances of the odour intensity do not need to be recorded at the same location.

Odour patrol was conducted by trained personnel/ competent persons with a specific sensitivity to a reference odour (i.e. on reference materials n-butanol with the concentration of 50ppm in nitrogen (v/v)) in compliance with Section 3.7.2 of the updated EM&A Manual patrolling and sniffing along the SENTX Site boundary to detect any odour.

The odour monitoring programme and patrol route are summarised in *Table 2.5* and illustrated in *Figure 2.2* respectively. Copies of the certificates of the qualified odour panelist are presented in *Annex D5*.

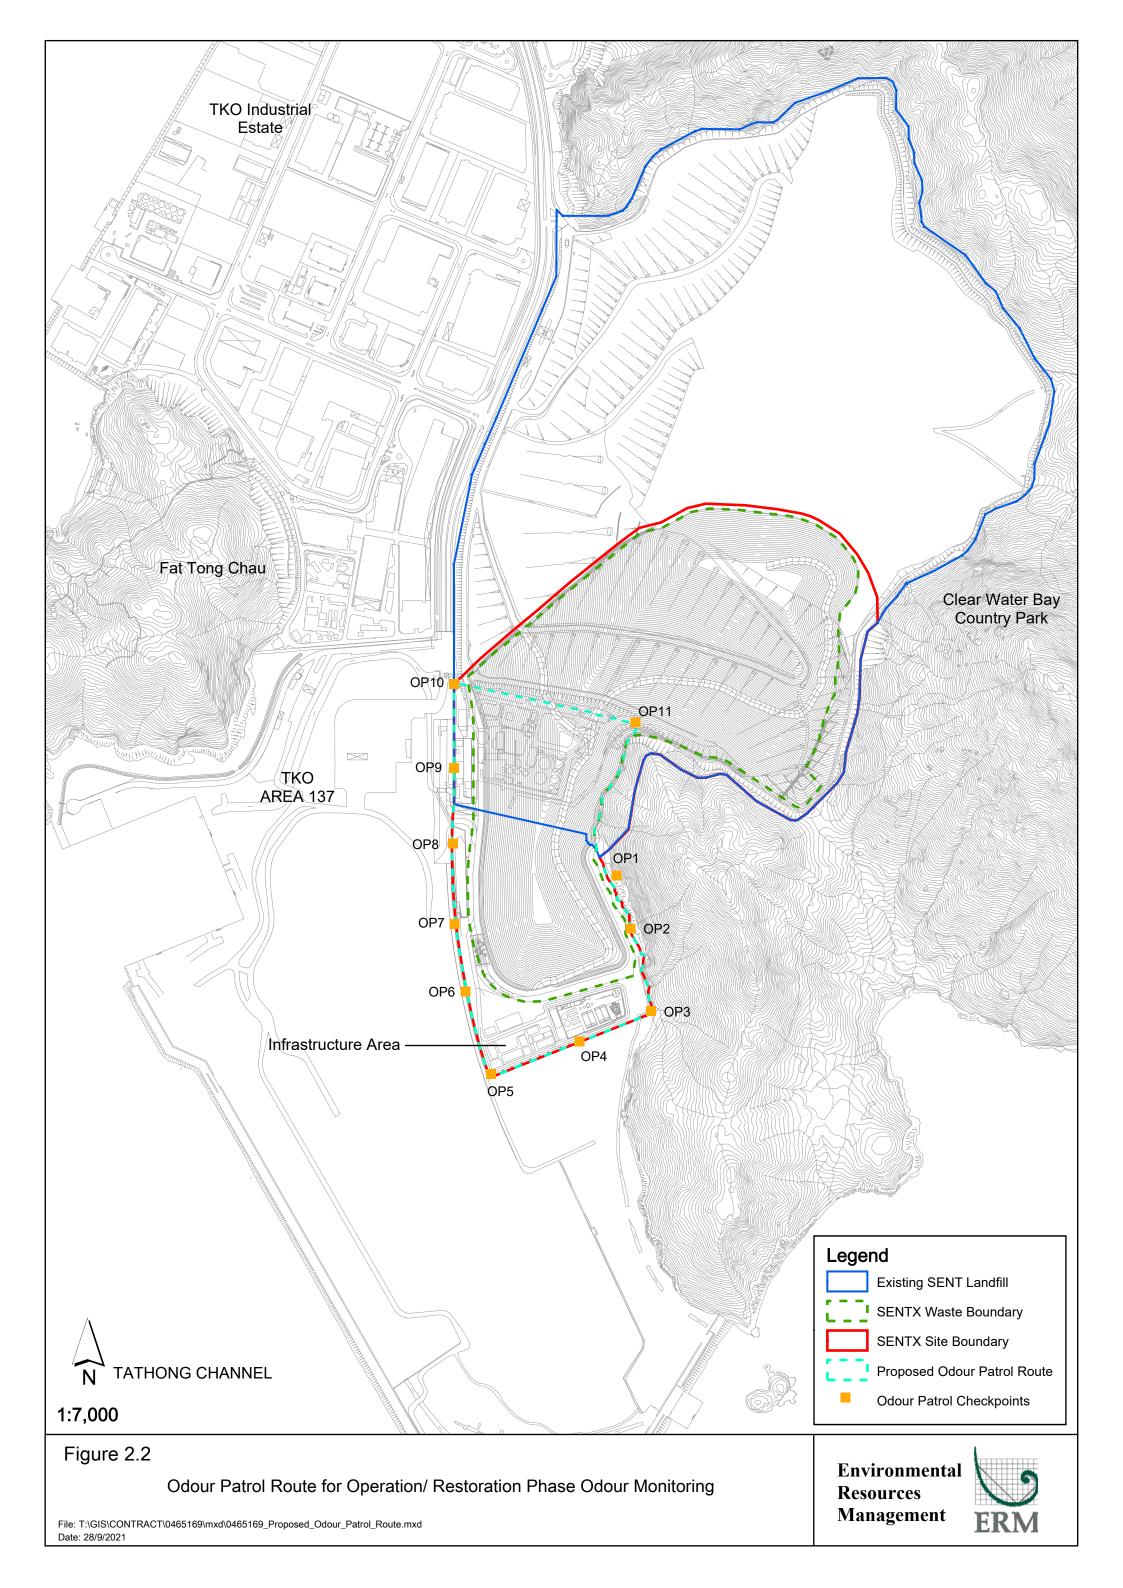


Table 2.5 Odour Monitoring Details

Patrol	Parameters	Patrol Frequency (a)	Monitoring Dates
Locations			
Patrol along the SENTX Site Boundary (Checkpoints OP1 - OP11)	Odour Intensity (see <i>Table 2.6</i>)	Period 1 - First month of operation Daily, three times a day in the morning, afternoon and evening/night (between 18:00 and 22:00 hrs) conducted by the ET and the IEC	Conducted by ET & IEC: 22 July 2022 Conducted by an
		Three times per week on different days conducted by an independent third party together with the ET and IEC (b)	independent third party, ET & IEC:
		Period 2 - Three months following period 1 (c)	
		Weekly conducted by the ET and the IEC	
		Once every two weeks conducted by an independent third party together with the ET and IEC (b)	
		Period 3 - Throughout operation following period 2 (c) Monthly conducted by the ET and the IEC	
Notoc		Quarterly conducted by an independent third party together with the ET and IEC (b)	

- (a) Reduction of monitoring frequency will be subject to the monitoring results to demonstrate environmentally acceptable performance.
- (b) Patrol shall be scheduled so that they are carried out together with the patrols to be carried out jointly by the ET and the IEC.
- (c) Commencement of each period will be justified by the ET Leader and verified by the IEC and will be subject to agreement with the EPD (EIAO Authority) and Project Proponent.

Table 2.6 Odour Intensity Level

Class	Odour Intensity	Description
0	Not Detected	No odour perceived or an odour so weak that it cannot be easily characterised or described.
1	Slight	Identified odour, slight
2	Moderate	Identified odour, moderate
3	Strong	Identified odour, strong
4	Extreme	Severe odour

Monitoring Schedule for the Reporting Month

The schedule for odour patrol during the reporting period is provided in *Annex C*.

The odour monitoring results are summarised and provided in *Table 2.7* and *Annex D6*, respectively.

Table 2.7 Summary of Odour Monitoring Results in the Reporting Period

Odour Checkpoints	Odour Intensity Class (Range)	Action Level	Limit Level
OP1	0	Odour intensity ≥	Odour intensity ≥
OP2	0	Class 2 recorded	Class 3 recorded
OP3	0		on 2 consecutive
OP4	0		patrol
OP5	0		
OP6	0		
OP7	0		
OP8	0		
OP9	0		
OP10	1		
OP11	0		

The potential odour source in the reporting period included the nearby operations of the Town Gas Plant. All the odour monitoring results were below the Action and Limit Levels in the reporting period. No action is thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex D3*.

2.1.3 Thermal Oxidiser, Landfill Gas Flare and Landfill Gas Generator Stack Emission Monitoring

Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, the performance of the thermal oxidiser, landfill gas flare and landfill gas generator was monitored when they are in operation. Gas samples were collected from the stack of the thermal oxidizer, landfill gas flare and landfill gas generator for laboratory analysis for NO₂, CO, SO₂, Benzene and Vinyl chloride and in-situ analysis for exhaust gas velocity at monthly interval and for laboratory analysis for non-methane organic compounds and ammonia (for thermal oxidizer only) at quarterly interval. The operating conditions of the thermal oxidiser, landfill gas flare and landfill gas generator were also monitored continuously.

The Limit Levels for stack emission of the thermal oxidiser, landfill gas flare and landfill gas generator are provided in Tables 2.8 - 2.10 below.

Table 2.8 Limit Levels for Stack Emission of the Thermal Oxidiser

Parameters	Limit Level
NO ₂	1.58 gs ⁻¹
CO	0.53 gs ⁻¹

Parameters	Limit Level
SO ₂	0.07 gs ⁻¹
Benzene	$3.01 \times 10^{-2} \text{ gs}^{-1}$
Vinyl chloride	$2.23 \times 10^{-3} \text{ gs}^{-1}$
Gas combustion temperature	850°C (minimum)
Exhaust gas exit temperature	443K (minimum) (a)
Exhaust gas velocity	7.5 ms ⁻¹ (minimum) ^(a)
Note:	
(a) Level under full load condition.	

 Table 2.9
 Limit Levels for Stack Emission of the Landfill Gas Flare

Parameters	Limit Level	
NO_2	0.97 gs ⁻¹	
CO	2.43 gs ⁻¹	
SO ₂	0.22 gs ⁻¹	
Benzene	$4.14 \times 10^{-4} \text{ gs}^{-1}$	
Vinyl Chloride	$2.60 \times 10^{-4} \text{ gs}^{-1}$	
Gas combustion temperature	815°C (minimum)	
Exhaust gas exit temperature	923 K (minimum) (a)	
Exhaust gas velocity	9.0 m s ⁻¹ (minimum) (a)	
Note:		
(a) Level under full load condition.		

Table 2.10 Limit Levels for Stack Emission of the Landfill Gas Generator

Parameters	Limit Level
NO ₂	1.91 gs ⁻¹
CO	2.48 gs ⁻¹
SO_2	0.528 gs ⁻¹
Benzene	2.47 x 10 ⁻⁴ gs ⁻¹
Vinyl chloride	$1.88 \times 10^{-5} \text{ gs}^{-1}$
Gas combustion temperature	450°C (minimum)
Exhaust gas exit temperature	723K (minimum) (a)
Exhaust gas velocity	30.0 ms ⁻¹ (minimum) ^(a)
Note:	
(a) Level under full load condition.	

Gas samples were collected from the centroid of the stack with stainless steel sampling probe, into inert sample containers (i.e. Canister and Tedlar Bag) and transferred to ALS Technichem (HK) Pty Ltd. (HOKLAS Registration No. 066) laboratory within 24 hours of collection for direct analysis on a gas chromatography within 48 hours after collection. The flue gas velocity of the gas stream at the exhaust of thermal oxidize was determined by S-Pitot tube during the emission sampling.

The stack emission monitoring programme and monitoring locations are summarised in *Table 2.11* and illustrated in *Figure 2.1*, respectively.

Table 2.11 Thermal Oxidiser, Landfill Gas Flare and Landfill Gas Generator Stack Emission Monitoring Details

Monitoring Location	Parameter	Frequency	Monitoring Date
Stack of Thermal Oxidiser	Laboratory analysis for • NO ₂	Monthly for the first 12 months of operation and thereafter at	
	• CO	quarterly intervals	
	• SO ₂	1	
	• Benzene		
	Vinyl chloride		
	In-situ analysis for		
	Exhaust gas velocity		
	Laboratory analysis for	Quarterly for the 1st	-
	Non-methane organic compounds	year of operation (b)	
	Laboratory analysis for	Quarterly	-
	• Ammonia		
	Gas combustion temperature	Continuously	1 - 31 July 2022
	• Exhaust temperature		
	Exhaust gas velocity (a)		
Stack of Landfill Gas	Laboratory analysis for	Monthly for the first 12 months of operation	12 July 2022
Flare	• NO ₂	and thereafter at	
	• CO	quarterly intervals	
	• SO ₂		
	• Benzene		
	 Vinyl chloride 		
	In-situ analysis for		
	Exhaust gas velocity		
	Laboratory analysis for	Quarterly for the 1 st year of operation (b)	-
	Non-methane organic compounds		
	 Gas combustion temperature 	Continuously	1 – 31 July 2022
	• Exhaust temperature		
	Exhaust gas velocity (a)		
Stack of Landfill Gas	Laboratory analysis for	Monthly for the first 12 months of operation	12 July 2022
Generator	• NO ₂	and thereafter at	
	• CO	quarterly intervals	
	• SO ₂		
	• Benzene		
	 Vinyl chloride 		
	In-situ analysis for		
	 Exhaust gas velocity 	Out of the	
	Laboratory analysis for	Quarterly for the 1st year of operation (b)	-
	Non-methane organic compounds	, car of operation (*)	

Monitoring Location	Parameter	Frequency	Monitoring Date
	Exhaust temperature	Continuously	1 - 31 July 2022
	Exhaust gas velocity (a)		

- (a) The exhaust gas velocity is calculated based on the cross-section area of the stack and continuous monitored gas flow and combustion temperature data.
- (b) The monitoring results will be reviewed towards the end of the first year of operation to determine if monitoring of this parameter can be terminated upon agreement by the EIAO Authority, IEC and Project Proponent.

Monitoring Schedule for the Reporting Month

The schedule for thermal oxidizer, landfill gas flare and landfill gas generator stack emission monitoring during the reporting period is provided in *Annex C*.

Results and Observations

The thermal oxidizer, landfill gas flare and landfill gas generator stack emission monitoring results and detailed continuous monitoring results are summarised in *Tables 2.12 - 2.14* and provided in *Annex D7*, respectively.

Table 2.12 Summary of Thermal Oxidiser Stack Emission Monitoring in the Reporting Period

Parameters	Monitoring Results (Range in Bracket)	Limit Level
NO_2	0.89 gs ⁻¹	1.58 gs ⁻¹
CO	<0.01 gs ⁻¹	0.53 gs ⁻¹
SO ₂	<0.01 gs ⁻¹	0.07 gs ⁻¹
Benzene	<2.1 x 10 ⁻⁴ gs ⁻¹	3.01 x 10 ⁻² gs ⁻¹
Vinyl chloride	$< 2 \times 10^{-5} \text{ gs}^{-1}$	2.23 x 10 ⁻³ gs ⁻¹
Gas combustion temperature	925°C (918°C - 934°C)	850°C (minimum)
Exhaust gas exit temperature	1,169K (1,162K - 1,175K)	443K (minimum) (a)
Exhaust gas velocity	9.7 ms ^{-1 (b)}	7.5 ms ⁻¹ (minimum) (a)

Notes:

- (a) Level under full load condition.
- (b) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring. The limit level was not applicable as the stack was not operated under full load condition.

Table 2.13 Summary of Landfill Gas Flare Stack Emission Monitoring in the Reporting Period

Parameters	Monitoring Results (Range in Bracket)	Limit Level
NO_2	<0.01 gs ⁻¹	0.97 gs ⁻¹
CO	0.53 gs ⁻¹	2.43 gs ⁻¹
SO_2	0.01 gs ⁻¹	0.22 gs ⁻¹
Benzene	<1.8 x 10 ⁻⁵ gs ⁻¹	$4.14 \times 10^{-4} \text{ gs}^{-1}$
Vinyl chloride	<1.4 x 10 ⁻⁵ gs ⁻¹	2.60 x 10 ⁻⁴ gs ⁻¹

Parameters	Monitoring Results (Range in Bracket)	Limit Level
Gas combustion temperature	Flare 1: 901°C (822°C - 955°C)	815°C (minimum)
	Flare 2: 855°C (824°C - 930°C)	
Exhaust gas exit temperature	Flare 1: 1,035K (963K - 1,083K)	923 K (minimum) (a)
	Flare 2: 1,093K (1,061K - 1,163K)	
Exhaust gas velocity	6.5 ms ^{-1 (b)}	9.0 m s ⁻¹ (minimum) ^(a)

- (a) Level under full load condition.
- (b) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring. The limit level was not applicable as the stack was not operated under full load condition.

Table 2.14 Summary of Landfill Gas Generator Stack Emission Monitoring in the Reporting Period

Parameters	Monitoring Results (Range in Bracket)	Limit Level
NO ₂	0.01 gs ⁻¹	1.91 gs ⁻¹
CO	0.28 gs ⁻¹	2.48 gs ⁻¹
SO_2	$0.003~{\rm gs}^{-1}$	0.528 gs ⁻¹
Benzene	<8.0 x 10 ⁻⁶ gs ⁻¹	2.47 x 10 ⁻⁴ gs ⁻¹
Vinyl chloride	<1.8 x 10-6 gs-1	$1.88 \times 10^{-5} \text{ gs}^{-1}$
Exhaust gas exit temperature	869K (848K - 893K)	723K (minimum) (a)
Exhaust gas velocity	11.2 ms ^{-1 (b)}	30.0 ms ⁻¹ (minimum) ^(a)

Note:

- (a) Level under full load condition.
- (b) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring. The limit level was not applicable as the stack was not operated under full load condition.

All thermal oxidizer, landfill gas flare and landfill gas generator stack emission monitoring results were below the Limit Levels in the reporting period. No action is thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex D3*.

2.2 Noise Monitoring

2.2.1 Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, impact noise monitoring was conducted weekly at the monitoring location (i.e. NM1) to obtain one set of 30-minute measurement between 07:00 and 19:00 hours on normal weekdays.

The Action and Limit Levels for operational noise of the Project are provided in *Table 2.15* below.

Table 2.15 Action and Limit Levels for Operational Noise

Time Period	Action Level (a)	Limit Level (b)
07:00 - 19:00 hrs on all days	When one documented complaint is received from any one of the noise	65 dB(A) at NSRs (c)
19:00 – 23:00 hrs on all days	sensitive receivers (NSRs) or	65 dB(A) at NSRs (c)
23:00 – 07:00 hrs on all days	75 dB(A) recorded at the monitoring station	55 dB(A) at NSRs (c)

- (a) 75dB(A) along and at about 100m from the SENTX site boundary was set as the Action Level.
- (b) Limits specified in the GW-TM and IND-TM for construction and operational noise, respectively.
- (c) Limit Level only apply to operational noise without road traffic and construction activities noise.

Noise monitoring was performed by ALS Technichem (HK) Pty Ltd. (HOKLAS Registration No. 066) using sound level meter at the designated monitoring station NM1 (see *Figure 2.1*) in accordance with the requirements stipulated in the updated EM&A Manual. Acoustic calibrator was deployed to check the sound level meter at a known sound pressure level. Details of the deployed equipment are provided in *Table 2.16*. Copies of the calibration certificates for the equipment are presented in *Annex E1*.

Table 2.16 Noise Monitoring Details

Monitoring Station (1)	Location	Parameter	Frequency and Duration	Monitoring Dates	Equipment
NM1	SENTX Site Boundary (North)	L _{eq (30 min)} measurement between 07:00 and 19:00 hours on normal weekdays (Monday to Saturday)	Once per week for 30 mins during operation of the Project	6, 12, 18, 25 July 2022	Sound Level Meter: Rion NL-52 (S/N: 00921191) Rion NL-52 (S/N: 00809405) Acoustic Calibrator:
					Rion NC-74 (S/N: 34246492) Bruel & Kjaer
					4231 (S/N: 2713428)

2.2.2 Monitoring Schedule for the Reporting Month

The schedule for noise monitoring during the reporting period is provided in *Annex C*.

2.2.3 Results and Observations

A total of 4 impact noise monitoring events were scheduled during the reporting period. Results for noise monitoring are summarised in *Table 2.17*. The monitoring results and the graphical presentation of the data are provided in *Annex E2*.

Table 2.17 Summary of Operation Noise Monitoring Results in the Reporting Period

Monitoring Station	Measured Noise Level L _{eq (30 min)} , dB(A)				
	Average	Range	Action and Limit Level		
NM1	52.9	51.5 - 54.4	75		

Major noise sources identified during the noise monitoring included noise from operations of the SENTX and the TKO Area 137 Fill Bank, aircrafts and insects.

No Action and Limit Levels exceedance was recorded for operation noise monitoring in the reporting period. No action is thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex E3*.

2.3 WATER QUALITY MONITORING

2.3.1 Surface Water Quality Monitoring

Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, impact surface water quality monitoring was carried out at the three designated surface water discharge points (i.e. DP3, DP4 and DP6) at monthly intervals during operation/ restoration phase to ensure that the SENTX will not cause adverse water quality impact. Suspension of impact surface water quality monitoring at DP3 was approved under the Baseline Monitoring Report by EPD on 24 July 2019 until the actual commencement of construction works affecting DP3 in 2022.

The parameters as listed in *Table 2.19* were determined by ALS Technichem (HK) Pty Ltd. (HOKLAS Registration No. 066).

The Limit Levels of the surface water quality impact monitoring are provided in *Table 2.18*.

Table 2.18 Limit Levels for Surface Water Quality

Parameters	Limit Level
DP4 & DP6	
Ammoniacal-nitrogen	>7.1 mg/L
COD	> 30 mg/L
SS	> 20 mg/L

Parameters	Limit Level
DP4 & DP6	

The limit levels specified for other parameters in *Table 10a of the Technical Memorandum Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters* shall also be followed.

The locations of the monitoring stations for the Project are shown in *Figure 2.1*. All *in situ* monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or other international accreditation scheme before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the surface water quality monitoring programme. Calibration for a DO meter was carried out before measurement according to the instruction manual of the equipment model. Details of the equipment used in the impact surface water quality monitoring works are provided in *Table 2.19*. Copies of the calibration certificates for the equipment are presented in *Annex F1*.

Table 2.19 Impact Surface Water Quality Monitoring Details

Monitoring Station	Location	Frequency	Monitoring Dates	Parameter		Equipment
DP4 DP6	Surface water discharge point DP4 Surface water	Monthly	25 July 2022	 pH Electrical conductivity (EC) DO SS COD 	BicarbonateChlorideSodiumPotassiumCalciumMagnesiumNickel	YSI Professional DSS (S/N: 15H103928)
	discharge point DP6			 BOD₅ TOC Ammoniacal -nitrogen Nitrate-nitrogen Nitrite-nitrogen TKN TN Phosphate Sulphate Sulphide Carbonate Oil & Grease 	 Manganese Chromium Cadmium Copper Lead Iron Zinc Mercury Boron 	
DP4 (Additional Monitoring)	Surface water discharge point DP4	Weekly	8 July 2022 15 July 2022	• SS		-

Monitoring Schedule for the Reporting Month

The schedule for surface water quality monitoring during the reporting period is provided in *Annex C*.

Results and Observations

One regular monitoring event for impact surface water quality monitoring was scheduled at all designated monitoring stations during the reporting period. However, sampling could not be carried out on 25 July 2022 due to insufficient flow. Details of impact water quality monitoring event are provided in *Annex F2*.

Limit Level exceedance (SS) was recorded for additional surface water quality impact monitoring on 30 June 2022 and the exceedance was found to be project-related upon further investigation. Actions in accordance with the Event and Action Plan in *Annex F3* were undertaken. Weekly additional surface water monitoring (SS) at DP4 were conducted on 8 July 2022 and 15

⁽a) Impact surface water quality monitoring at DP3 was suspended from the monitoring event on 25 July 2019 until the actual commencement of construction works affecting DP3 in 2022.

July 2022. The additional surface water monitoring results are summarized in *Table 2.20* below.

Table 2.20 Details of Additional Surface Water Quality Monitoring

Date	Monitoring Location	Parameter	Result	Limit Level	Remarks
8 July 2022	DP4	SS	26.3 mg/L	20 mg/L	Weekly monitoring shall be continued
15 July 2022	DP4	SS	7.1 mg/L	20 mg/L	Weekly monitoring was terminated

Limit Level exceedance was recorded for additional surface water quality monitoring at DP4 on 8 July 2022. Investigation of the exceedance was conducted and the investigation report is presented in *Annex F9*. Based on the investigation conducted for the monitoring event with potential Limit Levels exceedance with the Contractor, and the IEC, the SS exceedance at DP4 on 8 July 2022 was found deemed to Project-related activities.

The surface water monitoring results (SS) at DP4 on 15 July 2022 complied with the Limit Level as stipulated in the updated EM&A Manual and the weekly surface water monitoring (SS) at DP4 was terminated.

The Contractor was reminded to implement all relevant mitigation measures for the construction works and maintain good site practice. The ET will keep track on the monitoring data and ensure Contractor's compliance of the environmental requirements.

2.3.2 Leachate Monitoring

Monitoring Requirements and Equipment

According to the updated EM&A Manual, continuous monitoring of leachate level and daily monitoring of effluent quality were carried out during the operation/ restoration phase.

Reduction of effluent monitoring frequency (dry season) (from daily to monthly) was approved by EPD on 22 March 2022. Monthly effluent quality monitoring (dry season) shall be conducted from 23 March 2022.

Temperature, pH and volume of the effluent discharged from the leachate treatment plant were measured in-situ whereas the parameters as listed in *Table 2.21* were determined by ALS Technichem (HK) Pty Ltd. (HOKLAS Registration No. 066).

The Limit Levels of the leachate monitoring are provided in *Table 2.21*.

Table 2.21 Limit Levels for Leachate Levels and Effluent Quality

Parameters	Limit Level
Leachate Levels	
Leachate levels above the basal liner	1 m above the primary liner of the leachate containment system
Effluent Quality	
Temperature	> 43 °C
pH Value	6 – 10
Volume Discharged	>2,000 m ³
Suspended Solids (SS)	> 800 mg/L
Phosphate	> 25 mg/L
Sulphate	> 800 mg/L
Total Inorganic Nitrogen (a)	> 100 mg/L
Biochemical Oxygen Demand (BOD)	> 800 mg/L
Chemical Oxygen Demand (COD)	> 2,000 mg/L
Oil & Grease	> 20 mg/L
Boron	> 7,000 μg/L
Iron	> 5 mg/L
Cadmium	> 1 μg/L
Chromium	> 300 μg/L
Copper	> 1,000 μg/L
Nickel	> 700 μg/L
Zinc	> 700 µg/L

(a) Total Inorganic Nitrogen include Ammoniacal-nitrogen, Nitrite-nitrogen and Nitrate-nitrogen.

All *in situ* monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or other international accreditation scheme before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the leachate quality monitoring programme. Details of the equipment used are provided in *Table 2.22*. Copies of the calibration certificates for the equipment are presented in *Annex F4*.

Table 2.22 Leachate Levels and Effluent Quality Monitoring Details

Location	Frequency	Parameter	Monitoring Dates	Equipment
Leachate levels above the basal liner	Continuous	Leachate Levels	1 - 31 July 2022	Pairs of pressure transducers
Effluent discharged from LTP	Daily for the first 3 months upon full operation of the LTP at wet season (Apr to Sep) and dry season (Oct to Mar), respectively and reduce to monthly thereafter subject to the monitoring results of the first 3 months for each season and agreement with the EIAO Authority, IEC and IC. (a)	On-site Measurements: Volume pH Temperature Laboratory analysis: Suspended Solids COD BOD5 TOC Ammoniacal- nitrogen Nitrate-nitrogen Nitrite-nitrogen Sulphate Phosphate Oil & Grease Alkalinity Chloride Calcium Potassium Magnesium Iron Zinc Copper Chromium Nickel Cadmium Boron	1 - 31 July 2022	TOA HM- 30P (S/N: 790332) LUTRON WA-2017SD (S/N: T.016811)

Monitoring Schedule for the Reporting Month

The schedule for leachate monitoring during the reporting period is provided in *Annex C*.

Results and Observations

The leachate levels and effluent quality monitoring results are summarised in *Table 2.23* and *Table 2.24*, respectively. The detailed monitoring results are provided in *Annex F5* and *Annex F6*, respectively.

⁽a) Reduction of monitoring frequency will be subject to the monitoring results to demonstrate environmentally acceptable performance.

Table 2.23 Summary of Leachate Levels in the Reporting Period

Monitoring Location	Average Leachate Head Levels (cm) (Range in Bracket)	Limit Level (cm)
Pump Station No. 1X (Cell	1X)	
Meter No. X-1	58 (46 – 73)	> 178
Meter No. X-2	76 (66 – 88)	
Average	67 (56 – 80)	
Pump Station No. 2X (Cell	2X)	
Meter No. X-3	73 (57 – 86)	> 180
Meter No. X-4	78 (64 – 90)	
Average	75 (61 - 88)	
Pump Station No. 3X (Cell	3X)	
Meter No. X-5	68 (53 – 75)	> 175
Meter No. X-6	70 (62 – 75)	
Average	69 (62 – 75)	

Table 2.24 Summary of Effluent Quality Monitoring Results in the Reporting Period

Parameters		Monitori	ng Result	S	Limit Level
Effluent Discharged from LTP		Average	Min	Max	
Temperature	°C	33.7	25.0	38.1	> 43 °C
pH Value	pH unit	8.4	8.2	8.6	6 - 10
Volume Discharged	m^3	983.9	41.0	1552.0	>2,000 m ³
Suspended Solids (SS)	mg/L	29.8	7.6	95.2	> 800 mg/L
Phosphate	mg/L	4.6	2.0	6.5	$> 25 \mathrm{mg/L}$
Sulphate	mg/L	260.9	157.0	470.0	> 800 mg/L
Total Inorganic Nitrogen (a)	mg/L	52.2	43.2	68.5	> 100 mg/L
BOD	mg/L	8.1	3.0	13.0	> 800 mg/L
COD	mg/L	822.7	608.0	1040.0	> 2,000 mg/L
Oil & Grease	mg/L	< 5.0	< 5.0	< 5.0	$> 20 \mathrm{mg/L}$
Boron	μg/L	4796.2	3500.0	6020.0	$> 7,000 \mu g/L$
Iron	mg/L	1.5	<1.0	1.9	$> 5 \mathrm{mg/L}$
Cadmium	μg/L	<1.0	<1.0	<1.0	> 1 µg/L
Chromium	μg/L	102.7	67.0	133.0	> 300 μg/L
Copper	μg/L	14.9	<10.0	64.0	> 1,000 μg/L
Nickel	μg/L	101.7	62.0	127.0	> 700 μg/L
Zinc	μg/L	78.6	62.0	108.0	> 700 μg/L

All the leachate levels and effluent quality monitoring results were below the Limit Levels in the reporting period. No action is thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex F3*.

⁽a) Total Inorganic Nitrogen include Ammoniacal-nitrogen, Nitrite-nitrogen and Nitrate-nitrogen.

2.3.3 Groundwater Monitoring

Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project with incorporation of the proposed updates under the Amendment Summary approved by EPD on 15 June 2020, groundwater monitoring was carried out at 14 perimeter groundwater monitoring wells (including 3 up-gradient wells and 11 downgradient wells) (i.e. MWX-1 to MWX-14) to monitor the groundwater quality and level of the perimeter groundwater monitoring wells at monthly interval.

The Limit Levels for groundwater quality is provided in *Table 2.25* below.

Table 2.25 Limit Levels for Groundwater Quality

Location	Limit Levels			
	Ammoniacal-nitrogen (mg L-1)	COD (mg L-1)		
MWX-1	5.00	30		
MWX-2	5.00	30		
MWX-3	5.00	30		
MWX-4	7.63	36		
MWX-5	5.00	30		
MWX-6	5.00	46		
MWX-7	6.55	36		
MWX-8	15.85	50		
MWX-9	7.30	71		
MWX-10	5.00	30		
MWX-11	5.00	30		
MWX-12	5.00	30		
MWX-13	5.00	30		
MWX-14	5.00	30		

A bladder pump with Teflon sampling tube and adjustable discharge rates was used for purging and taking of groundwater sample from the monitoring wells. Filtered groundwater samples were collected by connecting a disposable in-line filter system to the tubing of the sampling pump, prior to storage and analysis by ALS Technichem (HK) Pty Ltd. (HOKLAS Registration No. 066).

A portable dip meter with 5mm accuracy was used for measurement of groundwater level at each well. The dip meter has an audio indicator of the water level and was checked before use.

The measurements of pH and electrical conductivity (EC) were undertaken *in situ*. *In situ* monitoring instruments in compliance with the specifications listed under Section 4.3.2 of the updated EM&A Manual were used to undertake the groundwater quality monitoring for the Project.

Details of the equipment used and the monitoring locations are summarised in *Table 2.26* and illustrated in *Figure 2.1*, respectively. Copies of the calibration certificates for the equipment are presented in *Annex F7*.

Table 2.26 Groundwater Monitoring Details

Monitoring Location	Frequency	Parameter		Monitoring Dates	Equipment
All groundwater monitoring wells (MWX-1 to MWX-14)	Monthly	 Water level pH EC COD BOD5 TOC Ammoniacal -nitrogen Nitrate-nitrogen Nitrite-nitrogen TKN TN Sulphate Sulphide Carbonate Bicarbonate Phosphate 	 Chloride Sodium Potassium Calcium Magnesium Nickel Manganese Chromium Cadmium Copper Lead Iron Zinc Mercury Boron 	4, 5 July 2022	YSI Professional DSS (S/N: 15H103928)

Monitoring Schedule for the Reporting Month

The schedule for surface water quality monitoring during the reporting period is provided in *Annex C*.

Results and Observations

The groundwater quality monitoring results and detailed monitoring results are summarised in *Table 2.27* and provided in *Annex F8*, respectively.

Table 2.27 Summary of Groundwater Monitoring Results in the Reporting Period

Location	Ammoniacal-nitroge	Ammoniacal-nitrogen (mg L-1)		
	Monitoring Results	Limit Levels	Monitoring Results	Limit Levels
MWX-1	0.26	5.00	26	30
MWX-2	0.21	5.00	6	30
MWX-3	1.12	5.00	15	30
MWX-4	2.00	7.63	16	36
MWX-5	0.55	5.00	12	30
MWX-6	3.25	5.00	32	46
MWX-7	4.85	6.55	35	36
MWX-8	14.00	15.85	42	50
MWX-9	0.63	7.30	60	71
MWX-10	< 0.01	5.00	15	30
MWX-11	0.02	5.00	9	30
MWX-12	0.01	5.00	<2	30
MWX-13	< 0.01	5.00	<2	30
MWX-14	<0.01	5.00	6	30

All the groundwater monitoring results were below the Limit Levels in the reporting period. No action is thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex F3*.

2.4 LANDFILL GAS MONITORING

2.4.1 Monitoring Requirements

According to the updated EM&A Manual of the Project, landfill gas monitoring was carried out at the perimeter of the waste boundary (monitoring wells), area between the SENTX Site boundary and the waste boundary (surface emission), occupied on-site building, service voids, utilities pit and manholes in the vicinity of the SENTX (build-up of landfill gas) during the operation/restoration phase.

The Limit Levels for landfill gas monitoring is provided in *Table 2.28* below.

Table 2.28 Limit Levels for Landfill Gas Constituents

Parameters	Monitoring Location	Limit Level (% (v/v))		
Perimeter Landfill Gas Mon	itoring Wells (a)			
Methane & Carbon Dioxide		Methane	Carbon Dioxide	
	LFG1	1.0	3.2	
	LFG2	1.0	4.3	
	LFG3	1.0	6.3	
	LFG4	1.0	7.0	
	LFG5	1.0	3.4	
	LFG6	1.0	9.1	
	LFG7	1.0	1.5	
	LFG8	12.6	2.4	
	LFG9	2.5	1.7	
	LFG10	3.5	1.6	

Parameters	Monitoring Location	Limit Level (% (v/v))		
	LFG11	3.0	2.0	
	LFG12	13.2	1.5	
	LFG13	22.5	2.7	
	LFG14	5.2	1.8	
	LFG15	18.2	2.0	
	LFG16	1.0	2.0	
	LFG17	17.8	2.4	
	LFG18	2.3	2.1	
	LFG19	6.3	3.1	
	LFG20	1.0	4.6	
	LFG21	1.0	4.8	
	LFG22	1.0	4.0	
	LFG23	1.0	10.3	
	LFG24	1.0	4.7	
	GP1	1.0	10.6	
	GP2 (shallow)	1.0	11.4	
	GP2 (deep)	1.0	10.4	
	GP3 (shallow)	1.0	6.9	
	GP3 (deep)	1.0	5.6	
	GP4 (shallow)	1.0	11.6	
	GP4 (deep)	1.0	7.7	
	GP5 (shallow)	1.0	10.8	
	GP5 (deep)	1.0	7.5	
	GP6	1.0	8.4	
	GP7	1.0	4.5	
	GP12	1.0	2.3	
	GP15	1.0	2.2	
	P7	1.0	2.5	
	P8	1.0	1.7	
	P9	1.0	2.7	
Service Voids, Utilities Pits a	and Manholes			
Methane (or flammable gas)	Service voids, utilities pits and manholes	1% by volum	ne	
Permanent Gas Monitoring S	System			
Methane (or flammable gas)	Permanent Gas Monitoring System	1% by volume (20% LEL)		
Area Between the SENTX Si	te Boundary and Waste F	Boundary (Surf	face Emission)	
Flammable gas	Area between SENTX site boundary and waste boundary	30 ppm		

Notes:

Gas analysers in compliance with the specifications listed under Section 5.4.1 of the updated EM&A Manual were used to monitor the gas parameters at the landfill gas monitoring wells, service voids, utilities pits and manholes. The gas analyser was calibrated by a laboratory accredited under HOKLAS at

⁽a) Limit Levels established based on the pre-operation phase baseline and additional landfill gas monitoring results in the Pre-operation Baseline Monitoring Report.

yearly intervals and checked before use to ensure the validity and accuracy of the results. A portable dip meter was used to monitor the water level in the monitoring wells.

Permanent gas monitoring systems with pre-set alarm levels for methane at 20% lower explosive limit (LEL, equivalent to 1% methane gas (v/v)) were installed and operated in all occupied on-site buildings at SENTX. A central control panel is equipped to alert site personnel when the gas concentration at any detector reaches the alarm level.

The equipment used in the landfill gas monitoring programme is summarised in *Table 2.29*. The landfill gas monitoring locations for perimeter landfill gas monitoring wells and service voids, utilities and manholes along the Site boundary are illustrated in *Figure 2.3* and *Annex G1*, respectively. Copies of the calibration certificates for the equipment are presented in *Annex G2*.

Table 2.29 Landfill Gas Monitoring Details

Monitoring Location	Frequency	Parameter	Monitoring Dates	Equipment
Perimeter landfill gas monitoring wells (LFG1 to LFG24, P7 to P9, GP1 to GP7, GP12 and GP15)	Monthly	MethaneCarbon dioxideOxygenAtmospheric pressure	12 July 2022	GA5000 (S/N: G507306)
Service voids, utilities and manholes along the Site boundary and within the SENTX Site (UU1 to UU28)	Monthly	MethaneCarbon dioxideOxygen	13 July 2022	GA5000 (S/N: G507306)
Permanent gas monitoring system in all occupied on-site buildings	Continuous	Methane (or flammable gas) by permanent gas monitoring system	1 - 31 July 2022	Permanent gas monitoring system

2.4.2 Monitoring Schedule for the Reporting Month

The schedule for landfill gas monitoring during the reporting period is provided in *Annex C*.

2.4.3 Results and Observations

The landfill gas monitoring results are summarised and provided in *Tables* 2.30 - 2.31 and Annex G3, respectively.

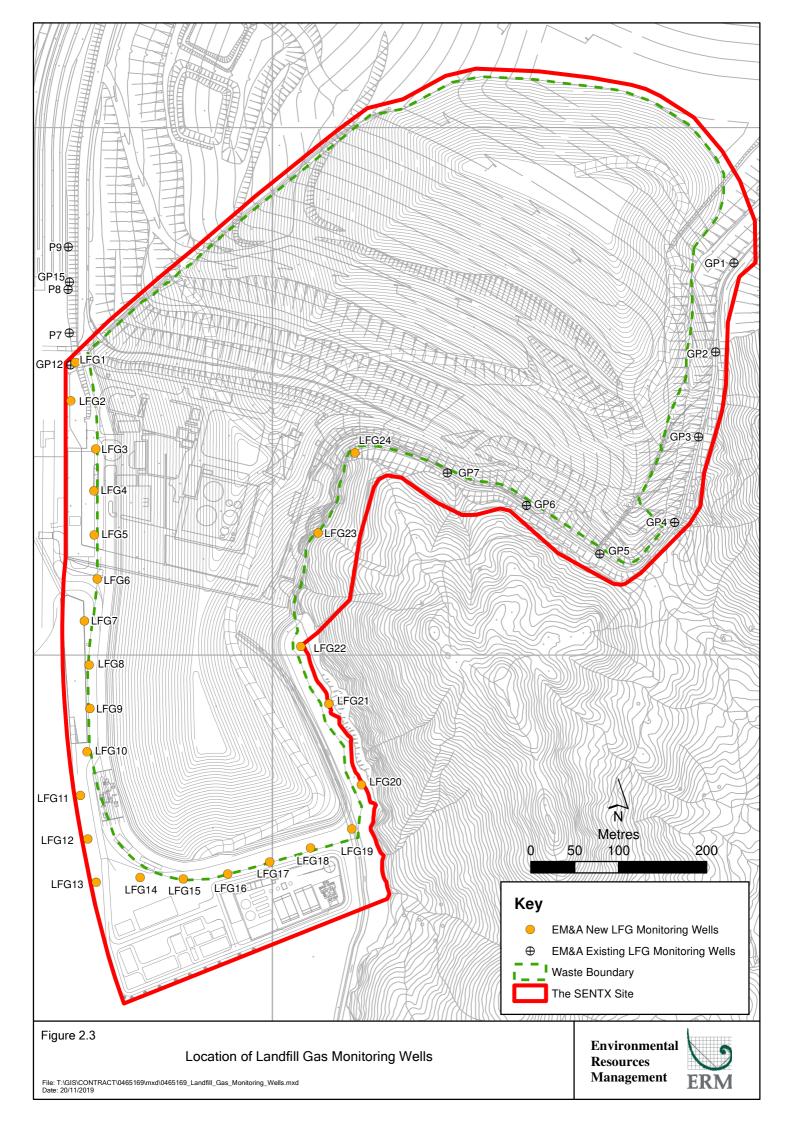


Table 2.30 Summary of Landfill Gas Monitoring Results at Perimeter LFG Monitoring Wells in the Reporting Period

Location	Methane (% (v	/v))	Carbon Dioxide (% (v/v))		
	Monitoring Limit Levels (a)		Monitoring Limit Lev		
	Results		Results		
LFG1	0.0	1.0	0.5	3.2	
LFG2	0.0	1.0	0.6	4.3	
LFG3	0.0	1.0	0.0	6.3	
LFG4	0.0	1.0	0.2	7.0	
LFG5	0.0	1.0	0.0	3.4	
LFG6	0.0	1.0	0.0	9.1	
LFG7	0.0	1.0	0.0	1.5	
LFG8	0.0	12.6	0.0	2.4	
LFG9	0.0	2.5	0.0	1.7	
LFG10	0.0	3.5	0.0	1.6	
LFG11	0.0	3.0	0.0	2.0	
LFG12	0.0	13.2	0.0	1.5	
LFG13	0.0	22.5	0.0	2.7	
LFG14	0.0	5.2	0.0	1.8	
LFG15	0.0	18.2	0.0	2.0	
LFG16	0.0	1.0	0.0	2.0	
LFG17	0.0	17.8	0.0	2.4	
LFG18	0.0	2.3	0.0	2.1	
LFG19	0.0	6.3	0.0	3.1	
LFG20	0.0	1.0	0.0	4.6	
LFG21	0.0	1.0	0.0	4.8	
LFG22	0.0	1.0	0.0	4.0	
LFG23	0.0	1.0	0.4	10.3	
LFG24	0.0	1.0	0.0	4.7	
GP1	0.2	1.0	3.4	10.6	
GP2 (shallow)	0.1	1.0	0.0	11.4	
GP2 (deep)	0.3	1.0	0.1	10.4	
GP3 (shallow)	0.0	1.0	0.4	6.9	
GP3 (deep)	0.0	1.0	0.5	5.6	
GP4 (shallow)	0.0	1.0	0.5	11.6	
GP4 (deep)	0.0	1.0	0.2	7.7	
GP5 (shallow)	0.0	1.0	5.0	10.8	
GP5 (deep)	0.0	1.0	0.1	7.5	
GP6	0.0	1.0	1.5	8.4	
GP7	0.0	1.0	1.4	4.5	
GP12	0.0	1.0	0.0	2.3	
GP15	0.0	1.0	0.0	2.2	
P7	0.0	1.0	0.0	2.5	
P8	0.0	1.0	0.0	1.7	
P9	0.0	1.0	0.0	2.7	

Notes:

⁽a) Limit Levels established based on the pre-operation phase baseline and additional landfill gas monitoring results in the Pre-operation Baseline Monitoring Report.

Table 2.31 Summary of Landfill Gas Monitoring Results at Service Voids, Utilities Pits and Manholes in the Reporting Period

Location	Methane (% (v/v))					
	Monitoring Results	Limit Levels				
UU01	0.0	1.0				
UU02	0.0	1.0				
UU03	0.0	1.0				
UU04	0.0	1.0				
UU05	0.0	1.0				
UU06	0.0	1.0				
UU07	0.0	1.0				
UU08	0.0	1.0				
UU09	0.0	1.0				
UU10	0.0	1.0				
UU11	0.0	1.0				
UU12	Voided due to latest site programme and on-going	1.0				
	operation work					
UU13	0.0	1.0				
UU14	0.0	1.0				
UU15	0.0	1.0				
UU16	0.0	1.0				
UU17	Voided due to latest site programme and on-going	1.0				
	operation work					
UU18	0.1	1.0				
UU19	0.0	1.0				
UU20	0.0	1.0				
UU21	0.0	1.0				
UU22	0.0	1.0				
UU23	0.0	1.0				
UU24	0.0	1.0				
UU25	0.0	1.0				
UU26	0.0	1.0				
UU27	0.0	1.0				
UU28	0.0	1.0				

The alarm of the permanent gas monitoring systems with pre-set levels for methane at 20% lower explosive limit (LEL, equivalent to 1% methane gas (v/v)) was not triggered at all occupied on-site buildings at SENTX in July 2022.

All the landfill gas monitoring results were below the Limit Levels in the reporting period. No action is thus required to be undertaken in accordance with the Event and Action Plan presented in *Annex G4*.

2.5 LANDSCAPE AND VISUAL MONITORING

2.5.1 Monitoring Requirements

According to the updated EM&A Manual of the Project, the monthly landscape and visual audit was conducted on 15 July 2022 to monitor the implementation of the landscape and visual mitigation measures during operation/ restoration phase.

All relevant environmental mitigation measures listed in the approved EIA Report and the updated EM&A Manual and their implementation status are summarised in *Annex B*.

2.5.2 Results and Observations

The Contractor has implemented environmental mitigation measures as stated in the approved EIA Report and the EM&A Manual.

Regarding the landscape and visual audit, the Contractor was reminded to maintain the advance screen planting works regularly to ensure effective screening of views of project works from the High Junk Peak Trail.

2.6 EM&A SITE INSPECTION

Site inspections were carried out on a weekly basis with the Contractor, IEC and ER to monitor the implementation of proper environmental pollution control and mitigation measures under the Project. In the reporting period, 4 site inspections were carried out on 7, 14, 21 and 28 July 2022.

Key observations during the site inspections are summarised in *Table 2.32*.

Table 2.32 Key Observations Identified during the Site Inspection in this Reporting Month

Inspection Date	Environmental Observations and Recommendations
7 July 2022	 The Contractor shall display NRMM labels on the excavator near X10c channel and generator near DP6 and replace the faded NRMM label on the excavator near DP3. The Contractor shall remove the general refuse accumulated at X10a channel regularly to ensure it is functioning properly at all times. The Contractor shall remove the stagnant water accumulated at the drip tray near LTP.
	• The Contractor shall provide surface water management at DP3 upstream to minimise SS runoff to the channel.
14 July 2022	 The Contractor shall display NRMM labels on the excavator at DP3 and roller near buttress wall. The Contractor shall remove/ cover the stockpile of dusty materials near DP3 to minimise dust impact. The Contractor shall provide surface water management at DP3 upstream to minimise SS runoff to the channel.
21 July 2022	 The Contractor shall remove the deposited silt and grit and stagnant water accumulated at DP3 sediment pit regularly to ensure it is functioning properly at all times. The Contractor shall remove the stagnant water accumulated in the manholes near channel X10C and spray larvicides for mosquito control, if necessary. The Contractor shall provide surface water management at DP3 upstream and cover the exposed slope to minimise SS runoff to the channel. The Contractor shall dispose of the empties chemical containers near DP3 as chemical waste in accordance with the COP.

Inspection Date	Environmental Observations and Recommendations
28 July 2022	The Contractor shall remove the deposited silt and grit and
	stagnant water accumulated at DP3 sediment pit regularly to
	ensure it is functioning properly at all times.
	 The Contractor shall remove the general refuse and stagnant
	water accumulated at the channel near sump house 3 to
	minimize odour and pest issues and spray larvicides for
	mosquito control, if necessary.
	• The Contractor shall provide surface water management at DP3
	upstream to minimise SS runoff to the channel.
	The Contractor shall remove the algae and scum in the Wetsep
	near DP4 to ensure it is functioning properly at all times.

The Contractor has rectified most of the observations identified during environmental site inspections in the reporting period. Key environmental deficiencies identified and the corresponding rectification actions are presented in *Table 2.33*.

Table 2.33 Summary of Environmental Deficiencies Identified and Corresponding Rectification Actions

Deficiencies	Rectifications Implemented	Proposed Additional Control Measures
Surface Water		
Intercepting channels & drainage system	Reviewed drainage plan.	 Addition of channels. Expedite the construction of permanent sediment trap and discharge culverts.
DP channels (design & regular silt removal)	 Carried out regular maintenance and cleaning of channels. DP4 channel: Area near the channel was paved with concrete and a bund was built. DP6 channel: Gravel piles on the channel were covered with concrete which serve as blocks for running water and to divide the channel into several sections. A pump was placed in the water zone in the upstream section to pump water to the Wetsep for treatment prior to the discharge to the last section before the weir plate. DP6: Pipes through the gravel piles between different channel sections were covered with geotextiles to block debris and silt. 	N.A.
Stockpiles & exposed soil	Installed silt fencing near surface water channel along DP6 channel.	 Improve soil covering. Compaction and cover for stockpiles and soil slopes.

Deficiencies	Rec	tifications Implemented	-	osed Additional rol Measures
Wetsep (treatment	•	Reviewed Wetsep capacity.	•	Install additional
capacity & number)	•	Chemicals dosage of the Wetsep was increased to enhance the efficiency.		Wetsep.
Backflow / ponding during heavy rainfall	•	Raised with EPD (LDG) and CEDD.	N.A.	

2.7 WASTE MANAGEMENT STATUS

The Contractor has registered as chemical waste producer under the Contract. Sufficient numbers of receptacles were available for general refuse collection and sorting.

As informed by the Contractor, waste generated during this reporting period include mainly Non-inert construction waste, Yard waste and Chemical waste. Reference has been made to the waste flow table prepared by the Contractor. The quantities of different types of wastes and imported fill materials are summarised in *Table 2.34*.

Table 2.34 Quantities of Different Waste Generated and Imported Fill Materials

Month/ Year	Inert C&D Materials (a) (in '000m³)	Impor Fill (in '00 (b) Rock	00kg)	Inert Construction Waste Re- used (in '000m³)	Non-inert Construction Waste (c) (in '000m³)	Recyclable Materials (d) (in '000kg)	Yard Waste (in '000kg)	Chemical Wastes (in '000kg)
1 - 31 July 2022	0	0	0	0	0.012	0	28.440	0.800

Notes:

- (a) Inert construction wastes include hard rock and large broken concrete, and materials disposed as public fill. Density assumption: 1.6 (kg/L) for public fill.
- (b) Imported fill refers to materials generated from other project for on-site reuse.
- (c) Non-inert construction wastes include general refuse disposed at landfill. Density assumption: 0.9 (kg/L) for general refuse.
- (d) Recyclable materials include metals, paper, cardboard, plastics and others.

2.8 IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

A summary of the Environmental Mitigation Implementation Schedule is presented in *Annex B*. The necessary mitigation measures were implemented properly for the Project.

2.9 SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMANCE LIMIT

The operation/ restoration phase noise and landfill gas monitoring results complied with the Action and Limit Levels in the reporting period. Two

exceedances of the Limit Level for air quality impact monitoring (TSP) and one exceedance of the Limit Level for surface water quality monitoring (SS) were recorded in the reporting period. The TSP exceedance at AM2 was considered Project-related while the exceedance at AM4 on 29 July 2022 was considered non-Project-related upon further investigation. The SS exceedance at DP4 on 8 July 2022 was considered Project-related upon further investigation.

Cumulative statistics on exceedances is provided in *Annex H*.

2.10 SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

There were no complaints, notification of summons or prosecution recorded in the reporting period.

Statistics on complaints, notifications of summons, successful prosecutions are summarised in *Annex H*.

3 FUTURE KEY ISSUES

3.1 CONSTRUCTION PROGRAMME FOR THE COMING MONTH

As informed by the Contractor, the major works for the Project in August 2022 will be:

- Defects rectification for waste reception area, including weighbridge, vehicle washing facilities, wheel wash bay and guard house;
- Defects rectification for infrastructure buildings;
- Defects rectification for surface water channels along the road pavement;
- Remaining civil work for Diesel Fuel Tank such as concrete staircase, handrails, pedestrian pavement in the proximity and canopy installation; and
- Landscaping work.

3.2 KEY ISSUES FOR THE COMING MONTH

Potential environmental impacts arising from the above upcoming construction activities in the next reporting period of August 2022 are mainly associated with potential surface water impact in the rainy season. The ET will keep track on the construction and operation works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

3.3 MONITORING SCHEDULE FOR THE COMING MONTH

The tentative schedule for environmental monitoring in August 2022 are provided in *Annex I*.

4 CONCLUSION AND RECOMMENDATION

This EM&A Report presents the findings of the EM&A activities undertaken during the period from 1 to 31 July 2022 in accordance with the updated EM&A Manual and the requirements of the Environmental Permit (*EP*-308/2008/B).

Air quality (24-hour TSP, odour, thermal oxidiser, landfill gas flare and landfill gas generator stack emission), noise, water quality (surface water, leachate and groundwater) and landfill gas monitoring were carried out in the reporting period. Results for air quality (odour, thermal oxidiser, landfill gas flare and landfill gas generator stack emission), noise, water quality (leachate and groundwater) and landfill gas monitoring complied with the Action and Limit Levels in the reporting period. Two exceedances of the Limit Level for TSP and one exceedance of the Limit Level for surface water quality (SS) were recorded in the reporting period.

Environmental site inspections were carried out during the reporting period. Recommendations on remedial actions were given to the Contractor for the deficiencies identified during the site inspections.

There were no complaints, notification of summons or prosecution recorded in the reporting period.

The ET will keep track on the construction and operation/restoration works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Annex A

Work Programme

SA25 Construction (Initial Montes)	1153 12-Apr-18 07-Jun-21 705		
SA2.5 Construction (Initial Works) SA2.5.02 Advance Works & Site Establishment SA2.5.02.01 Site Establishment & Mobilization 5.02.01 52-1000 Site Mobilization for Parts X1 & X2	1148 12-Apr-18 02-Jun-21 35 333 12-Apr-18 10-Mar-19 820	FS, M 3. 1: FS, M 3. 2: FS	
5.02.01 52-1100 Site Mobilization for Parts X3, X4 & X5 5.02.01 52-1200 Temporary Office for Employer / ER / IC	30 12-Apr-18 11-May-18 1083 11-1300: FS, 11-1400: FS, 11-1500: FS 52-1300: F 60 10-Oct-18 08-Dec-18 0 23-1300: FS 11-1700: S	FS, M 3. 1: FF SS, M 3. 1: FS	
5.02.01 52-1300 Hoarding and Fencing Works SA2.5.02.02 Site Survey & Investigation Works for Parts X1 & X2 5.02.02 52-1400 Condition Survey	40 30-Jan-19 10-Mar-19 820 52-1000: FS, 52-1100: FS 32-1500: FS 50 31-Dec-18 18-Feb-19 840 25 31-Dec-18 24-Jan-19 840 11-1100: FS, 11-1200: FS 52-1600: FS	FS, M10. 1: FS -26, M10. 2: FS -13, M10. 3: FS FS	
5.02.02 52-1500 Topographic Survey 5.02.02 52-1600 Site inspection, Review of Condition Survey Report	20 31-Dec-18 19-Jan-19 845 11-1100: FS, 11-1200: FS 52-1600: F 25 25-Jan-19 18-Feb-19 840 52-1500: FS, 52-1400: FS 32-1500: F	FS	
SA2.5.02.03 Site Survey & Investigation Works for Parts X3, X4 & X5 5.02.03 52-1700 Condition Survey 5.02.03 52-1800 Topographic Survey	50 12-Apr-18 31-May-18 1103 25 12-Apr-18 06-May-18 1103 11-1300: FS, 11-1400: FS, 11-1500: FS 52-1900: F 20 12-Apr-18 01-May-18 1108 11-1300: FS, 11-1400: FS, 11-1500: FS 52-1900: F	FS	
5.02.03 52-1900 Site inspection, Review of Condition Survey Report SA2.5.02.04 Environmental Monitoring 5.02.04 52-2000 Installation of Monitoring Stations & Wells (GP & GW)	25 07-May-18 31-May-18 1103 52-1700: FS, 52-1800: FS 32-1500: FS 975 02-Oct-18 02-Jun-21 35 120 02-Oct-18 29-Jan-19 0 23-1600: FS 52-2200: S	SS 60	
5.02.04 52-2100 Installation of Monitoring Stations & Wells (GP & GW) on Buttress Wall 5.02.04 52-2200 Conduct Baseline Monitoring for Construction (one month) 5.02.04 52-2300 Conduct Baseline Monitoring for Operation (one year)	120 02-Oct-18 29-Jan-19 0 23-1600: FS 52-2200: S 30 01-Dec-18 30-Dec-18 0 52-2000: SS 60, 52-2100: SS 60 11-1100: F 365 03-Jun-20 02-Jun-21 35 32-1500: FS -400, 53-4500: FS 12-1400: F	FS	
SA2.5.03 Civil Engineering Works SA2.5.03.0 Buttress Wall 5.03.0 53-1000 Section adj. SENT		FS, 53-1300: FS, 53-3100: FS, M 3. 5: FS -150, M 3.	
5.03.0 53-1100 Diversion of SENT Landfill Gas Pipe 5.03.0 53-1200 Section at Cell 4	11-1400: FS 7: FS 45 07-Feb-20 22-Mar-20 96 23-2500: FS, 53-1000: FS 53-1300: F	FS, 54-4000: FS, M 3. 3: FS FS, 53-3100: FS, M 3. 6: FS -200	
5.03.0 53-1300 Install Landfill Gas Pipe on Buttress Wall SA2.5.03.1 Landfill Cell 1	75 05-Apr-20 18-Jun-20 83 41-1500: FS, 53-1100: FS, 53-1200: FS, 53-1000: FS 54-4000: F	FS	
5.03.1 53-1400 Earth bund (Eastern)	90 04-Aug-19 01-Nov-19 9 11-1100: FS, 23-2500: FS, 53-4200: FS, 53-2800: FS 63-1100: F	FS, 53-2300: FS, 53-3400: FS, 63-1000: FS, FS, 63-1200: FS, 63-1200: FS, 63-1300: FS, M 4. 2: FS	
5.03.1 53-1500 Earth bund (Southern) 5.03.1 53-1600 Earth bund (Western)	53-3700: F	FS, 53-2200: FS, 53-2300: FS, 53-3400: FS, FS, 53-3800: FS FS, 53-2000: FS, 53-2200: FS, 53-3800: FS	
5.03.1 53-1700 Intercell bund (Cell 1/2) 5.03.1 53-1800 Site Formation	75 13-Jan-19 28-Mar-19 432 11-1100: FS, 23-2500: FS 53-2000: FS 90 13-Jan-19 12-Apr-19 217 11-1100: FS, 23-2500: FS, 31-1300: FS 53-1900: FS 45	FS, 63-1100: FS, 63-1200: FS, 63-1300: FS, M 4. 1:	
5.03.1 53-1900 Pump Station (PS#1X) 5.03.1 53-2000 Lining Works		FS, 53-2200: FS	
5.03.1 53-2100 Protective Stone Laying & Leachate Collection Pipe 5.03.1 53-2200 Install Leachate Force Main	75 16-Mar-20 29-May-20 214 53-2000: FS, 41-1500: FS, 53-1900: FS 32-1500: FS 75 25-Jul-19 07-Oct-19 449 53-1500: FS, 53-1600: FS, 41-1500: FS, 53-1900: FS 54-2800: F	FS, 54-2800: FS, M 4. 3: FS FS	
5.03.1 53-2300 Install Landfill Gas Pipe on earth bund 5.03.1 53-2400 Leachate Pipe Connection (Cell 1 to LTP) SA2.5.03.4 Landfill Cell 4	55 02-Nov-19 26-Dec-19 258 41-1500: FS, 53-1400: FS 54-4000: FS 30 09-Mar-20 07-Apr-20 266 23-2500: FS, 54-1000: SS 54-2800: FS 30 09-Jul-20 07-Aug-20 144		
SA2.5.03.4 Landfill Cell 4		FS, M 3. 3: FS FS	
5.03.5 53-2600 Construct Cut-Off Channel 12A 5.03.5 53-2700 Connect Cut-Off Channel 12A to DP6 5.03.5 53-2800 Diversion from Existing Trapezoidal Channel into Channel 12A	20 17-Mar-19 05-Apr-19 9 53-2600: FS, 31-1400: FS, 23-1900: FS 53-2800: F 20 06-Apr-19 25-Apr-19 9 53-2700: FS 53-1400: FS		
5.03.5 53-2900 Removal of Existing Trapezoidal Channel along Eastern Bund 5.03.5 53-3000 Cut-Off Channel C4 Diversion to Cut-Off Channel 17-2	30 26-Apr-19 25-May-19 9 53-2800: FS 53-4200: FS 53-42	FS FS, 53-1200: FS	
5.03.5 53-3100 Cut-Off Channel X5 on Buttress Wall, Cell 4, Cell 3 5.03.5 53-3200 Temporary Diversion Cut-Off Channel X5 to 12A 5.03.5 53-3300 Culvert X5 (5m long) & Perm Connection of Cut-Off Channel X5	90 05-Apr-20 03-Jul-20 289 53-1000: FS, 53-1200: FS 20 04-Jul-20 23-Jul-20 289 53-3100: FS, 23-1900: FS 30 26-Dec-20 24-Jan-21 134 53-4100: FF, 63-1900: FS, 53-3200: FS 32-1500: F	FS, M 3. 4: FS	
5.03.5 53-3400 Construct Perimeter Channel X6 on Eastern Bund & Southern Bund of Cell 1 5.03.5 53-3500 Construct Perimeter Channel X6 on Eastern Bund of Cell 2 5.03.5 53-3600 Construct Perimeter Channel X6 Eastern Bund of Cell 3	50 02-Nov-19 21-Dec-19 249 53-1400: FS, 53-1500: FS 53-3500: FS 53-3500: FS 50 20-Feb-20 09-Apr-20 189 63-1000: FS, 53-3400: FS 53-3600: FS 50 09-Jun-20 28-Jul-20 129 63-1900: FS, 53-3500: FS 53-3900: FS 53-3900: FS	FS FS	
5.03.5 53-3700 Culvert X6 (25m long) at Cell 1 Southern Bund 5.03.5 53-3800 Perimeter Channel (X9B) at Cell 1 Southern & Western Bund	75 25-Jul-19 07-Oct-19 1314 53-1500: FS 45 25-Jul-19 07-Sep-19 1344 53-1500: FS, 53-1600: FS		
5.03.5 53-3900 Drop Inlet & Culvert (X9) - 21m long 5.03.5 53-4000 Sediment Trap (ST)	2: FS	FF, 53-4100: FF, 53-6000: FS, M 9. 1: FS -90, M 9. FS, M 9. 3: FS -90, M 9. 4: FS	
5.03.5 53-4100 Dual Culvert 74m long (connect to DP4) SA2.5.03.6 Drainage - Ground Water	200 26-May-19 11-Dec-19 209	FF, 53-6000: FS, M 9. 1: FS -90, M 9. 2: FS	
5.03.6 53-4200 Construct Groundwater Collection Pipe along Cells X1 & X2 Eastern Bund 5.03.6 53-4300 Construct Groundwater Collection Pipe along Cell X3 Eastern Bund	70 26-May-19 03-Aug-19 9 11-1100: FS, 23-1600: FS, 53-2900: FS 53-1400: F 50 04-Aug-19 22-Sep-19 159 53-4200: FS 53-4400: F	FS, 53-4300: FS, 63-1000: FS, 63-1900: FS FS, 63-1900: FS	
5.03.6 53-4400 Construct Groundwater Collection Pipe along Intercell Bund X2/X3 5.03.6 53-4500 Construct Manhole MH-X1 SA2.5.03.7 Utilities - Distribution within New Infrastructure Area	30 12-Nov-19 11-Dec-19 209 53-4400: FS 52-2300: F 391 11-Aug-19 04-Sep-20 276	FS, 63-1200: FS FS, M 9. 5: FS	
5.03.7 53-4600 Power Supply HV Works (Transformer & HV switchgear) 5.03.7 53-4700 Power Distribution, LV Power Supply Works	5 30-Jun-20 04-Jul-20 0 54-3000: FS 12-1200: F 2 05-Jul-20 06-Jul-20 0 54-3100: FS, 12-1200: FS 12-1000: F		
5.03.7 53-4800 Sewerage (Collection to LTP) 5.03.7 53-4900 Sewerage (Discharge to Site Boundary) 5.03.7 53-5000 Lighting Provision	60 07-Jul-20 04-Sep-20 271 54-1000: FS, 54-4100: FS, 54-4600: FS 12-1100: F	FS, 53-6100: FS FS, 53-6100: FS FS, 32-2100: FS	
5.03.7 53-5100 Fire Services 5.03.7 53-5200 Water Supply (Fresh & Salt)	115 12-Mar-20 04-Jul-20 2 53-6800: FS 12-1000: F 115 12-Mar-20 04-Jul-20 338 53-6600: FS, 53-6700: FS 12-1100: F	FS FS	
5.03.7 53-5300 Telecom & Network 5.03.7 53-5400 Gas Network (LFG to LTP) SA2.5.03.8 Utilities - Works Associated with Utilities Undertakers	45 11-Aug-19 24-Sep-19 622 53-6400: FS 12-1100: F 15 22-Jun-20 06-Jul-20 176 54-1000: FF 54-2800: F 703 27-Feb-19 29-Jan-21 129		
SA2.5.03.8.U1 CLP 5.03.8.U1 53-5500 Excavate Trench for CLP Cable	459 27-Feb-19 30-May-20 43 100 13-May-19 20-Aug-19 194 23-2900: FS 53-5800: FS	FS, 54-1000: SS, 54-4100: SS, 54-4600: SS, M10. 0, M10. 2: FS -30, M10. 3: FS	
5.03.8.U1 53-5600 Backfill Trench after CLP Cable Laying 5.03.8.U1 53-5700 CLP Cable Laying (from CLP Substation to Site Boundary) 5.03.8.U1 53.5800 CLP Cable Laying (from Site Boundary to HV Suitebroom)	200 27-Feb-19 14-Sep-19 229 32-2400: FS 54-3000: F		
5.03.8.U1 53-5800 CLP Cable Laying (from Site Boundary to HV Switchroom) 5.03.8.U1 53-5900 CLP HV associated equipment installation SA2.5.03.8.U2 DSD	120 18-Dec-19 15-Apr-20 0 54-2900: FS , 32-2400: FS 53-5800: F	FS, 54-3000: FS FF 15	
SA2.5.03.8.U2 DSD 5.03.8.U2 53-6000 Connection to Storm Drain System 5.03.8.U2 53-6100 Connection to Foul Drain System	147 05-Sep-20 29-Jan-21 129 5 25-Jan-21 29-Jan-21 129 53-4100: FS, 53-4000: FS, 53-3900: FS 32-1500: F 5 05-Sep-20 09-Sep-20 271 53-4800: FS, 53-4900: FS 32-1500: F		
SA2.5.03.8.U3 Telecom 5.03.8.U3 53-6200 Excavate Trench for PCCW		FS, 54-1000: SS, 54-4100: SS, 54-4600: SS, M10. 0, M10. 2: FS -20, M10. 3: FS	
5.03.8.U3 53-6300 Backfill Trench after PCCW Cable Laying 5.03.8.U3 53-6400 Laying Cables & Connection SA2.5.03.8.U4 WSD		FF, 54-4100: FF, 54-4600: FF FS, 53-6300: FS	
SA2.5.03.8.U4 WSD 5.03.8.U4 53-6500 Install Watermain & Piping for Water Supplies 5.03.8.U4 53-6600 Connection for Fresh Water & Meter Installation	, , , , , , , , , , , , , , , , , , ,	FS, 53-6700: FS, 53-6800: FS, 53-6900: FS FS	
5.03.8.U4 53-6700 Connection for Salt Water 5.03.8.U4 53-6800 Connection for Fire Services 5.03.8.U4 53-6900 Connection for Cooling Tower & Meter Installation	30 11-Feb-20 11-Mar-20 338 53-6500: FS, 32-2300: FS 53-5200: FS 30 11-Feb-20 11-Mar-20 2 53-6500: FS, 32-2300: FS 53-5100: FS	FS	
SA2.5.03.8.U5 HyD Lighting 5.03.8.U5 53-7000 Installation of Public Street Lighting / Handover	120 07-Jul-20 03-Nov-20 216 120 07-Jul-20 03-Nov-20 216 54-4100: FS, 54-4600: FS, 54-1000: FS 32-1500: F		
SA2.5.04 Building Construction, incl. E&M and System Installation, and T&C SA2.5.04.A Part X1 Area A 5.04.A General Area & Access Road	53-6300: FF, 12-1000: FF, 11-1100: FS, 54-1100: FF, 53-5000: F	FS, 53-2400: SS, 53-4800: FS, 53-4900: FS, FS, 53-5400: FS, 68-1700: FS	
5.04.A 54-1100 Carpark & Supporting Area 5.04.A 54-1200 Diesel Fuel Tanks	54-1800: FF	FS, M 5.11: FS -30, M 5.12: FS, 54-1000: FF, FS	
5.04.A 54-1300 EPD Building	270 30-Apr-19 24-Jan-20 44 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1700: SS 60 32-2100: F 54-1400: S	FS, M 5. 4: FS -135, M 5. 5: FS, 12-1000: FS, SS 60	
5.04.A 54-1400 Fire Service Tank 5.04.A 54-1500 GVL Building		FS, M 5.10: FS, 12-1000: FS, 54-1600: SS 60 FS, M 5. 1: SF 30, M 5. 2: SF 150, M 5. 3: FS,	
5.04.A 54-1600 Laboratory Building 5.04.A 54-1700 Maintenance Building & Area	270 28-Aug-19 23-May-20 44 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1400: SS 60 32-2100: F 32-2200: F 270 01-Mar-19 25-Nov-19 44 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1500: SS 60 32-2100: F 32-	FS, M 5. 6: FS -135, M 5. 7: FS, 12-1000: FS, FS FS, M 5. 8: FS -135, M 5. 9: FS, 12-1000: FS,	
5.04.A 54-1800 Storage Facility & Area	54-1300: S 60 01-Mar-19 29-Apr-19 64 23-1300: FS, 11-1100: FS, 54-1100: FS 54-2000: F	SS 60 FS, M 5.11: FS -30, M 5.12: FS, 54-1000: FF, FS	
5.04.A 54-1900 Waste Oil Tanks 5.04.A 54-2000 Water Service House		FS, M 5.10: FS, 12-1000: FS, 54-4400: FS	
SA2.5.04.B Part X1 Area B SA2.5.04.B.1 BioPlant Building 5.04.B.1 54-2100 LTP BioPlant Building	890 31-Dec-18 07-Jun-21 0 330 17-Jan-19 12-Dec-19 243 330 17-Jan-19 12-Dec-19 243 243 23-1300: FS, 23-5200: FS, 23-3200: FS, 11-1100: FS, 31-1000: FS 32-2100: FS	FS, 32-2200: FS, M 6. 2: FS -165, M 6. 3: FS	
SA2.5.04.B.2 Leachate Treatment Plant 5.04.B.2 54-2200 Main Plant Area included Civil works	589 31-Dec-18 10-Aug-20 21 274 31-Dec-18 30-Sep-19 0 23-1300: FS, 23-3200: FS, 11-1100: FS 54-2300: F	FS, 54-2400: FS, 54-2500: FS, 64-1100: FS, M 6. 1: 6. 4: FS -137, M 6. 5: FS	
5.04.B.2 54-2300 MEP Installation 5.04.B.2 54-2400 SBR Tanks	11-1100: FS M 6. 9: FS	FS 60, 32-1900: FS, 54-2600: FS, M 6. 8: FS -110, S, 32-2200: FS FS, M 6. 6: FS	
5.04.B.2 54-2400 SBR Tanks 5.04.B.2 54-2500 Ammonia Stripper SA2.5.04.B.3 LTP - Test & Commission 5.04.B.3 54-2600 Dry testing	315 01-Oct-19 10-Aug-20 21 41-3000: FS, 54-2200: FS 54-2600: FS 301 11-Aug-20 07-Jun-21 0	FS, M 6. 8: FS -150, M 6. 9: FS FS -150, 23-6900: SS, 54-2700: FS, M11, 1: FS	
5.04.B.3 54-2700 Wet testing	75 25-Sep-20 08-Dec-20 21 54-2600: FS, 12-1200: FS, 53-6900: FS, 31-2200: FS, 23-6800: FS	FS, M11. 2: FS	
5.04.B.3 54-2800 Operational testing SA2.5.04.C Part X1 Area C	160 30-Dec-20 07-Jun-21 0 54-2700: FS, 53-2400: FS, 53-2500: FS, 53-2100: FS, 53-2500: FS, 53-25	FS, M11. 3: FS, M11. 4: FS	
SA2.5.04.C.1 LFG - Power Supply Building 5.04.C.1 54-2900 LFG Building (with Transformer Room)	530 17-Jan-19 29-Jun-20 5 335 17-Jan-19 17-Dec-19 0 23-1300: FS, 23-3500: FS, 11-1100: FS, 31-1000: FS 53-5800: FS	FS, 53-5900: FS, 54-3000: FS, 54-3100: FS, M 7. 6:	
5.04.C.1 54-3000 Transformer & HV Swtichgear Installation 5.04.C.1 54-3100 MEP Installation, with T&C		FS, M 7. 4: FS -30, M 7. 5: FS, M 7. 5: FF FS, 32-2100: FS, 53-4700: FS, 53-4800: FS, M 7. 4: 17. 5: FS	
SA2.5.04.C.2 LFG Treatment Plant 5.04.C.2 54-3200 Main Plant Area included Civil Works	554 31-Dec-18 06-Jul-20 0 54-3300: FS, 11-1100: FS 54-3300: FS	FS, 54-3400: FS, 54-3500: FS, 54-3600: FS, FS, 54-3600: FS, FS, 54-3800: FS, M 7. 1: SF 30, M 7. 2: FS -200, M	
5.04.C.2 54-3300 MEP Installation 5.04.C.2 54-3400 GHS600 Blower 601 A&B Relocation	170 19-Jan-20 06-Jul-20 0 54-3200: FS, 12-1000: FF 32-2000: FS	FS, 53-4800: FS, 54-3900: FS, M 7. 4: FS -80, M 7. FS, M 7. 4: FS -8, M 7. 5: FS	
5.04.C.2 54-3500 Pre-treatment 5.04.C.2 54-3600 Flares (incl. PLC control, interlink to Towngas PF & LTP)	60 19-Jan-20 18-Mar-20 110 41-3900: FS, 54-3200: FS 54-3900: FS 125 19-Jan-20 22-May-20 45 41-3300: FS, 54-3200: FS 54-3900: F	FS, M 7. 4: FS -60, M 7. 5: FS FS, M 7. 4: FS -60	
5.04.C.2 54-3700 LFG Engine (incl. on-grid protection, PLC control, turning) 5.04.C.2 54-3800 Cooling System SA2.5.04.C.3 LFG - Test & Commission 5.04.C.3 54-3900 MEP Testing	45 19-Jan-20 03-Mar-20 125 22-1500: FS , 54-3200: FS 54-3900: F	FS, M 7. 4: FS -25, M 7. 5: FS	
5.04.C.3 54-3900 MEP Testing 5.04.C.3 54-4000 Operational Testing	54-3800: FS, 12-1200: FS, 53-6900: FS, 31-2200: FS, 54-3300: FS 111 10-Sep-20 29-Dec-20 0 53-1300: FS, 63-2700: FS, 63-1800: FS, 53-2300: FS, 32-1500: F	FS, 54-2800: FS, 63-4800: FF, 63-4900: FS,	
SA2.5.04.D Part X1 Area D 5.04.D 54.4100 General Area & Access Road	53-1100: FS, 54-3900: FS, 23-7200: FS 63-4600: F	FS, 53-4800: FS, 53-4900: FS, 53-5000: FS,	
5.04.D 54-4100 General Area & Access Road 5.04.D 54-4200 VWF Building	53-6300: FF, 12-1000: FF, 11-1100: FS 53-7000: F 120 28-Oct-19 24-Feb-20 63 23-1300: FS, 23-5200: FS, 41-4500: FS, 11-1100: FS, 32-2100: F	FS, M 8. 5: FS FS, M 8. 4: FS, M 8. 6: FS -60, M 8. 7: FS, 12-1000:	
5.04.D 54-4300 Weighbridge	54-4300: SS 60 FS, 54-450 75 29-Aug-19 11-Nov-19 63 41-4200: FS, 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-4400: SS 60 85, 54-4500 85, 54-	500: SS 60 FS, M 8. 6: FS -40, M 8. 7: FS, 54-4200: SS 60	
5.04.D 54-4400 Weighmaster House 5.04.D 54-4500 Wheel Wash Bath		FS, M 8. 1: FS, 12-1000: FS, 54-4300: SS 60 FS, M 8. 3: FS, 12-1000: FS, 54-4700: SS 30	
SA2.5.04.E Part X1 Area E & Part X2 5.04.E 54-4600 General Area & Access Road	163 26-Jan-20 06-Jul-20 6	FS, 53-4900: FS, 53-5000: FS, 53-7000: FS	
5.04.E 54-4700 Guard House & Entrance Gate SA2.5.08 Landscape Works - Advance Screen Planting in CWB Country Park	100 26-Jan-20 04-May-20 63 23-1300: FS, 23-5200: FS, 11-1100: FS, 11-1200: FS, 54-4500: SS 30 32-2100: F	FS, M 8. 2: FS, 12-1000: FS	
SA2.5.08.N Area N 5.08.N 58-1000 Advance Screen Planting	270 01-Apr-19 26-Dec-19 529 90 01-Apr-19* 29-Jun-19 529 23-7900: FS, 31-1100: FS, 11-1500: FS 14-1800: S	SS -60, 58-1100: SS, 68-1600: SS 30, M 3. 2: FS	
5.08.N 58-1100 Establishment of Screen Planting SA2.5.08.S Area S 5.08.S 58-1200 Advance Screen Planting		SS, M 3. 2: FS	
5.08.S 58-1300 Establishment of Screen Planting SA2.6 Construction (Remaining Works) SA2.6.02 Advance Works	270 01-Apr-19* 26-Dec-19 529 58-1200: SS 32-1500: F 1474 01-Apr-19 13-Apr-23 30 80 09-Jul-21 26-Sep-21 339	·S	
	80 09-Jul-21 26-Sep-21 339 23-2100: FS, 12-1300: FS 23-2000: S 60 09-Jul-21 06-Sep-21 239 32-2100: FS, 12-1300: FS 23-2000: S	SS -90, 63-2800: FS, 63-2900: FS, 63-3000: FS, FS, M12. 4: FS -30, M12. 5: FS	
SA2.6.02.9 Demolition of SENT Infrastructure Area 6.02.9 62-1000 Existing SENT General Infrastructure Facility & Building			
		FS, 63-4500: FS, M12. 4: FS -30, M12. 5: FS FS, 63-4500: FS, M12. 4: FS -30, M12. 5: FS	
6.02.9 62-1000 Existing SENT General Infrastructure Facility & Building 6.02.9 62-1100 Existing SENT LTP 6.02.9 62-1200 Existing SENT LFG Remaining Work			Date Revision Checked 11-May-18 SENTX-GVL-W-PB-ZZ-0001 Rev. I01

# 17	WBS Path		Activity A	activity Name	Dur	0	tart Finis	sh Total Pr	redecessor Details	Successor Details
500			ID ,	,	1050			Float		
510	SA2	.6.03.2	Civil Enginee Landfill Cell	2	449	02-Nov	-19 13-Apr-2 -19 23-Jan-2	21 810		
511	6.00	3.2	63-1000 Ea	arth bund (Eastern)	110	02-Nov	-19 19-Feb-2		3-2800: FS	53-3500: FS, 63-1500: FS, 63-1800: FS, 63-1900: FS, 63-2000: FS, 63-2100: FS, 63-2200: FS, M12. 1: FS -50, M12.
										2: FS, 63-1100: FS
512	6.03	3.2	63-1100 Ea	arth bund (Western)	110	20-Feb	-20 08-Jun-2			63-1400: FS, 63-1500: FS, 63-1700: FS, 63-3500: FS, 63-3600: FS, 63-1200: FS
513	6.03	3.2	63-1200 In	ntercell bund (Cell 2/3)	90	09-Jur	1-20 06-Sep-2	20 734 11	1-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: FS,	63-1500: FS
514	6.03	3.2	63-1300 Si	Site Formation	75	02-Nov	-19 15-Jan-2		3-4400: FS, 63-1100: FS 1-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: FS	63-1400: FS, 63-4200: FS
5	<u> </u>									·
515			63-1400 Pt 63-1500 Lii	Pump Station (PS#2X)						63-1600: FS, 63-1700: FS 63-1600: FS, M12. 3: FS, 63-2400: FS
310										, ,
517				Protective Stone Laying & Leachate Collection Pipe					3-1500: FS, 41-1500: FS, 63-1400: FS	32-1600: FS, M12. 3: FS
519				nstall Leachate Force Main stall Landfill Gas Pipe on earth bund						54-2800: FS, M12. 3: FS 54-4000: FS, M12. 3: FS
520			Landfill Cell	<u>'</u>			-20 25-War-2 -20 02-Feb-2		1 1000.1 0 ₁ 00° 1000.1 0	51 1000. 1 G, W12. G. 1 G
521				arth bund (Eastern)				20 9 11		53-3300: FS, 53-3600: FS, 63-2400: FS, 63-2700: FS, M12. 1: FS -50, M12. 2: FS, 63-2000: FS -45, 63-2200: FS
								53	3-2800: F5, 63-4200: F5	F5 -50, M12. 2: F5, 63-2000: F5 -45, 63-2200: F5
522	6.00	3.3	63-2000 Ea	arth bund (Western)	110	25-Ap	-20 12-Aug-2	20 19 11	1-1100: FS, 63-1000: FS, 63-1900: FS -45	63-2300: FS, 63-2400: FS, 63-2600: FS, 63-3700: FS, 63-2100: FS -45
523	6.03	3.3	63-2100 In	ntercell bund (Cell 3/4)	105	29-Jur	ı-20 11-Oct-2	20 789 11	1-1100: FS, 63-1000: FS, 63-4200: FS, 63-2000: FS -45	63-2400: FS
524		0.0	00,0000 0:	N. E. C.	75	00.1	00 00 4 (20 0 44	4 4400 50 00 4000 50 00 4000 50	20,0000 50
524			63-2200 Si	Pump Station (PS#3X)						63-2300: FS 63-2500: FS, 63-2600: FS
526			63-2400 Lii							63-2500: FS, M12. 3: FS
020	0.00	0.0	03-2400 Eli	illing Works	100	01-000	21 00-0411-2		3-1500: FS	·
527				Protective Stone Laying & Leachate Collection Pipe						32-1700: FS, M12. 3: FS
528				nstall Leachate Force Main					3-2000: FS, 41-1500: FS, 63-2300: FS	53-2500: SS -90, 54-2800: FS, M12. 3: FS
530			Landfill Cell	nstall Landfill Gas Pipe on earth bund			-20 13-Jul-2 -21 13-Apr-2		1-1500: FS, 63-1900: FS	54-4000: FS, M12. 3: FS
531				Remaining Portion of Buttress Wall			-21 13-Apr-2 -21 04-Jan-2		2-1000: FS	
532	6.03	3.4	63-2900 Ea	arth bund (Western) incl. MSE Wall	120	07-Sep	-21 04-Jan-2	22 239 62		63-3000: FS, 63-3100: FS, 63-3200: FS, 63-3400: FS,
										63-3800: FS, 63-3900: FS, 63-4100: SS -90, M 9. 6: FS -60, M 9. 7: FS -30, M 9. 8: FS
Foo		2.4	00.000	NA Famatia		05 :	.00 0411	000		
533	6.03	ა.4	63-3000 Si	oile Formation	120	05-Jar	-∠∠ 04-May-2		2-1000: FS, 62-1100: FS, 62-1200: FS, 63-2900: FS, 3-4100: FS	63-3100: FS
534	6.03	3.4	63-3100 Pt	Pump Station (PS#4X)	45	05-May	-22 18-Jun-2	22 239 63	·	63-3300: FS, 63-3400: FS
535			63-3200 Lii						·	63-3300: FS, M12. 6: FS
536				Protective Stone Laying & Leachate Collection Pipe					· · · · · · · · · · · · · · · · · · ·	12-1900: FS, 32-1800: FS, M12. 6: FS
537				nstall Leachate Force Main & Remove Temporary Leachate Pipe					1-1500: FS, 63-2900: FS, 63-3100: FS	12-1900: FS, 32-1800: FS, M12. 6: FS
538 539				Surface Run-Off Perimeter Channel (X9A) at Cell 2 Western Bund			-20 03-Feb-2 -20 23-Jun-2		3-1100: FS	12-1900: FS
540				Perimeter Channel (X10A) at Cell 2 Western Bund			-20 08-Jul-2			63-4000: FS
541				Perimeter Channel (X10A) at Cell 3 Western Bund			-20 11-Sep-2			63-4000: FS
542				Perimeter Channel (X10A) at Cell 4 Western Bund			-22 24-Jan-2			63-4000: FS
543	6.03	3.5	63-3900 Pe	Perimeter Channel (X10C) at Cell 4 Western Bund	15	05-Jar	-22 19-Jan-2	22 469 63	3-2900: FS	63-4000: FS
544	6.03	3.5	63-4000 C	Connection to Existing DP3	10	25-Jar	-22 03-Feb-2	22 464 63	3-3900: FS, 63-3600: FS, 63-3700: FS, 63-3800: FS	12-1900: FS
545	6.03	3.5	63-4100 R	Remove Cut-Off Channel C-7 at bottom of Buttress Wall	30	09-Jur	-21 08- Jul-	21 419 63	3-2900: SS -90	63-3000: FS
546				emporary Channel (X7T) at SENT Infrastructure Area			-20 14-Feb-2			63-1900: FS, 63-2100: FS
547				Ground Water			-21 30-Nov-2			00 1000110100
548				Construct Temporary Channel (TC-1), from MH-1 to Existing UC-825						63-4400: FS
549				Divert GW at MH-1 to TC-1			:-21 31-Oct-2			63-4500: FS, M 9. 9: FS
550				Reconnection of GWCP across Cell 4					2-1100: FS, 62-1200: FS, 63-4400: FS	12-1900: FS
551 552			Utilities - Wo 8.U1 CLP	orks Associated with Utilities Undertakers			-20 27-Jul- -20 27-Jul-			
553				FG Generator On-grid Testing					<u> </u>	63-4700: FS
554				FG Generator On-grid Inspection & Verify			-21 27-Jul-2		3-4600: FS	12-1900: FS
555 556	SA	<mark>2.6.03.8</mark> റ3 മ പര	8.U6 TownGa	aying Gas Mains (from LFG to Town Gas PF)	55 45	15-Nov	-20 08-Jan-2 -20 29-Dec-2	21 855 20 855 54	4-4000: FF	63-4900: FS
557				Gas Meter Relocation & Connection at LFG						12-1900: FS
558	- T		Building & E8				:-19 22-Jul-2			
559	SA2	.6.04.C	Part X1 Area	а С	661	01-Oc	:-19 22-Jul-2	21 660		
560 561				eatment Plant GHS600 Blower 601 C Relocation			:-19 22-Jul-2 I-21 22-Jul-2			12-1900: FS
562				Absorption Chiller (Optional)			:-19 29-Dec-1			12-1900: FS
563			Landscape W				-19 03-Dec-2			
564	SA2	.6.08.1	SENT Area -	Tree Removal & Transplanting			26-Nov-1		4 4000, 50	20.4400 F0.20.4000 F0.20.4400 F0
565				Access trees condition and select for transplanting			19* 30-Apr-1			68-1100: FS, 68-1200: FS, 68-1400: FS
567				Prepare new site to receive trees		-	-19 29-Jul-			68-1200: SS 68-1300: FS
569				ransplant selected trees Prune trees prior to removal from Cell 4			-19 28-Aug-1 -19 26-Nov-1		, , , , , , , , , , , , , , , , , , ,	68-1300: FS 12-1900: FS
JUN				rene Felling - Part X3		_				12-1900: FS
569	6.08	8.1	68-1400 Tr	U		ay				
569 570				- Trial Nursery & Tree Planting	583	01-May	-19 03-Dec-2	20 891		
569 570 571	SA2 .	2 .6.08.2 8.2	SENTX Area		300	01-May	-19 24-Feb-2	20 1174 14		12-1900: FS, M 3. 2: FS 12-1900: FS

Annex B

Environmental Mitigation Implementation Schedule

Annex B Environmental Mitigation Implementation Schedule

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
Air Quali	ty - Cons	struction Phase						
4.8.1	AQ1	Blasting	To minimise	Blasting area	SENTX	✓	Air Pollution Control	Not applicable.
		• The area within 30m of the blasting area will be wetted prior to blasting.	potential dust nuisance	and 30m of blasting area	Contractor		(Construction Dust) Regulations	Blasting is not required in the latest landfill design
		 Blasting will not be carried out when the strong wind signal or tropical cyclone warning signal No. 3 or higher is hoisted, unless this is with the express prior permission of the Commissioner of Mines. 						· ·
		 loose material and stones in the Site will be removed prior to the blast operation 						
		 During blasting, blast nets, screens and other protective covers will be used to prevent the projection of flying fragments and material resulting from blasting 						
4.8.1	AQ2	Rock Drilling	To minimise	Rock drilling	SENTX	✓	Air Pollution Control	Not applicable.
		 Watering will be carried out at the rock drilling activities to avoid fugitive dust emissions. 	potential dust anuisance	area	Contractor		(Construction Dust) Regulations	Rock drilling is not required in the latest landfill design
4.8.1	AQ3	Site Access Road	To minimise	Main haul	SENTX	✓	Air Pollution Control	Reminder was given

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		The main haul road will be kept clear of dusty materials or sprayed with water.	potential dust nuisance	road	Contractor		(Construction Dust) Regulations	to the Contractor
		The main haul road will be paved with aggregate or gravel.					HKAQO and EIAO-TM Annex 4	
		• Vehicle speed will be limited to 10kph.						
4.8.1	AQ4	Stockpiling of Dusty Materials	To minimise	All	SENTX	✓	Air Pollution Control	Deficiency of
		Any stockpile of dusty materials will be covered entirely by impervious sheeting	potential dust nuisance	construction works area	Contractor		(Construction Dust) Regulations	mitigation measures but rectified by the Contractor
		or placed in an area sheltered on the top and three sides or sprayed with water so as to ensure that the entire surface is wet.					HKAQO and EIAO-TM Annex 4	
4.8.1	AQ5	<u>Loading, unloading or transfer of dusty</u> <u>materials</u>	To minimise potential dust	All construction	SENTX Contractor	✓	Air Pollution Control (Construction Dust) Regulations	Implemented
		 All dusty materials will be sprayed with water immediately prior to any loading, unloading or transfer operation so as to maintain the dusty material wet. 	nuisance	works area			HKAQO and EIAO-TM Annex 4	
4.8.1	AQ6	Site Boundary and Entrance	To minimise	Site boundary	SENTX	✓	Air Pollution Control	Not applicable
		Where a site boundary adjoins a road, street, service lane or other area accessible	potential dust nuisance	and entrance	Contractor		(Construction Dust) Regulations	
		to the public, hoarding of height not less than 2.4m from ground level will be provided along the entire length of that portion of the site boundary except for the site entrance or exit.					HKAQO and EIAO-TM Annex 4	
4.8.1	AQ7	Excavation Works	To minimise	All	SENTX	✓	Air Pollution Control	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		Working area of any excavation or earth moving operation will be sprayed with water immediately before, during and immediately after the operation so as to ensure that the entire surface is wet.	potential dust nuisance	construction works area	Contractor		(Construction Dust) Regulations HKAQO and EIAO-TM Annex 4	
4.8.1	AQ8	 Building Demolition The area where the demolition works are planned to take place will be sprayed with water immediately prior to, during and immediately after the demolition activities. Any dusty materials remaining after a stockpile is removed will be wetted with water and cleared from the surface of roads or street. 	To minimise potential dust nuisance	All construction works area	SENTX Contractor	✓	Air Pollution Control (Construction Dust) Regulations HKAQO and EIAO-TM Annex 4	Implemented
4.8.1	AQ9	 Construction of the Superstructure of Building Effective dust screens, sheeting or netting will be provided to enclose the scaffolding from the ground level up to the highest level of the scaffolding. 	To minimise potential dust nuisance	All construction works area	SENTX Contractor	✓	Air Pollution Control (Construction Dust) Regulations HKAQO and EIAO-TM Annex 4	Implemented
4.8.1	AQ10	Should a stone crushing plant be needed on site, the control measures recommended in the Best Practicable Means Requirement for Mineral Works (Stone Crushing Plants) BPM 11/1 should be implemented.	To minimise potential dust nuisance	Stone crushing plant/ construction phase	SENTX Contractor	✓	Best Practicable Means Requirement for Mineral Works (Stone Crushing Plants) BPM 11/1	Not applicable. Stone crushing plant is not required in the latest landfill design

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	imp mea	plement the asure? (1)	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
4.8.1	AQ11	Good site practices such as regular maintenance and checking of the diesel powered mechanical equipment will be adopted to avoid any black smoke emissions and to minimize gaseous emissions.	To minimise potential dust nuisance	All construction works area	SENTX Contractor		✓	HKAQO and EIAO-TM Annex 4	Implemented
4.10.1	AQ12	Dust monitoring once every 6 days	Ensure the dust generated from the project meets the air quality requirement	At monitoring locations shown in <i>Figure 3.2a</i>	SENTX Contractor		√	HKAQO and EIAO-TM Annex 4	Implemented
Air Quali	ty - Oper	ation, Restoration and Aftercare Phases							
4.8.2	AQ13	Odour • Enclosing the weighbridge area	To minimise odour nuisance	Weighbridge area	SENTX Contractor	√	~	EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only which is significantly less odorous, enclosing the weighbridge area is not necessary
4.8.2	AQ14	• Providing a vehicle washing facility before the exit of SENTX and providing sufficient signage to remind RCV drivers to pass through the facility before leaving SENTX		Vehicle washing facility	SENTX Contractor	✓	~	EIAO-TM Annex 4	Implemented
4.8.2	AQ15	Reminding the RCV drivers to empty the liquor collection sump and close the valve	To minimise odour nuisance	Tipping face	SENTX Contractor		~	EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste

EIA Ref.	EM&A Ref		nvironmental Protection Measures/ Aitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
			before leaving the tipping face						only, which is relatively dry, the amount of liquor generated is expected to minimal
4.8.2	AQ16	•	Washing down the area where spillage of RCV liquor is discovered promptly	To minimise odour nuisance	SENTX Site	SENTX Contractor	√	EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only, which is relatively dry, the amount of liquor generated is expected to minimal.
4.8.2	AQ17	•	Reminding operators to properly maintain their RCVs and ensure that liquor does not leak from the vehicles		SENTX Site	SENTX Contractor	✓	EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only, which is relatively dry, the amount of liquor generated is expected to minimal.
4.8.2	AQ18	•	Installation of landfill gas control system to enhance collection of landfill gas from the waste mass and hence minimise odour associated with fugitive landfill gas emissions	To minimise odour nuisance	SENTX Site	SENTX Contractor	√ ✓ ✓	EIAO-TM Annex 4	Implemented

EIA Ref.	EM&A Ref		nvironmental Protection Measures/ Iitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	im	easu	nent (1)			What requirements or standards for the measure to achieve?	Implementation Status and Remarks
4.8.2	AQ19	•	Progressive restoration of the areas which reach the finished profile (a final capping system including an impermeable liner will be put in place) and installation of a permanent landfill gas extraction system	To minimise odour nuisance	SENTX Site	SENTX Contractor	✓		✓	✓	,	EIAO-TM Annex 4	Implemented
4.8.2	AQ20	•	Installing deodorizers along the site boundary adjacent to the ASRs	To minimise odour nuisance	SENTX Site boundary	SENTX Contractor			✓	•		EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only which is significantly less odorous, installation of deodorizers is not necessary.
4.8.2	AQ21	•	Erecting a vertical barrier, wall or structure softened by planting rows of trees/shrubs or landscape feature along the site boundary, particularly in the areas near the ASRs		SENTX Site boundary	SENTX Contractor	✓		✓	~	,	EIAO-TM Annex 4	Implemented
4.8.2 and SENTX latest design	AQ22	•	Maintaining the size of the active tipping face not greater than 1,200 m ²	To minimise odour nuisance	Active tipping face	SENTX Contractor			✓			EIAO-TM Annex 4	Implemented
4.8.2	AQ23	•	Promptly covering the MSW with soil or selected inert materials to control odour emissions	To minimise odour nuisance	Active tipping face	SENTX Contractor			✓			EIAO-TM Annex 4	Not Applicable. SENTX will not receive MSW.

EIA Ref.	EM&A Ref		nvironmental Protection Measures/ litigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
4.8.2	AQ24	•	Maintaining the size of the special waste trench not greater than 6m (l) \times 2.5m (w)	To minimise odour nuisance	Special waste trench	SENTX Contractor	✓	EIAO-TM Annex 4	Not Applicable. SENTX will not have any special waste trench.
4.8.2 and SENTX latest design	AQ25		Covering daily covered area with a tarpaulin sheet or 300mm of soil after the landfill operating hours	To minimise odour nuisance	Daily covered area	SENTX Contractor	✓	EIAO-TM Annex 4	Implemented
4.8.2	AQ26	•	Covering special waste trench with 600 mm of soil and an impervious liner after 5 pm	To minimise odour nuisance	Special waste trench	SENTX Contractor	✓	EIAO-TM Annex 4	Not Applicable. SENTX will not have any special waste trench.
4.8.2	AQ27		Covering the non-active tipping face with 600mm of soil and an impermeable liner (on top of the intermediate cover), which will not only control odour emissions from landfilled waste but also enhance landfill gas extraction by the landfill gas extraction system	To minimise odour nuisance	Intermediate cover	SENTX Contractor	~	EIAO-TM Annex 4	Implemented
4.8.2	AQ28	•	Applying deodorizers or odour suppression agents to control odour emissions from the active tipping face and special waste trench, if any, through spraying or fogging equipment	To minimise odour nuisance	Active tipping face and special waste trench	SENTX Contractor	✓	EIAO-TM Annex 4	Not Applicable. As SENTX will receive construction waste only which is significantly less odorous, installation of deodorizers is not necessary.

EIA Ref.	EM&A Ref	Mitigation Measures Re Mo	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When implemeasu	ment th re? ⁽¹⁾		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
										Moreover, SENTX will not have any special waste trench.
4.8.2	AQ29	 Providing a mobile cover with retractable or suitable opening to cover up the opening of the special waste trench except during waste deposition and a suitable odour removal unit. The mobile cover should be equipped with powered extraction and suitable odour removal unit for purifying the trapped gas inside the trench before release into the atmosphere 	To minimise odour nuisance	Special waste trench	SENTX Contractor		√		EIAO-TM Annex 4	Not Applicable. SENTX will not have any special waste trench.
4.8.2 and SENTX latest design	AQ30	Providing a thermal oxidizer for the leachate treatment plant	To minimise odour nuisance as a result of breakdown of thermal oxidizer	Leachate treatment plant	SENTX Contractor	✓	✓	√	EIAO-TM Annex 4	Implemented
4.8.2 and SENTX latest design	AQ31	• Enclosing all the leachate storage and treatment tanks (except for the Sequential Batch Reactor (SBR) or Membrane Bioreactor (MBR) tanks) and diverting the exhaust air from these tanks to a thermal oxidizer or flare to avoid potential odour emissions from the LTP	To minimise odour nuisance	Leachate treatment plant	SENTX Contractor	✓	✓	✓	EIAO-TM Annex 4	Implemented
4.8.2	AQ32	Rescheduling of waste filling activities on- site by avoiding waste filling activities	To minimise odour nuisance	SENTX Site	SENTX Contractor		✓		EIAO-TM Annex 4	Not Applicable. As SENTX will receive

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		carrying out at the northern area of the site in the summer months between July to November						construction waste only which is significantly less odorous, rescheduling of waste filling activities is not necessary.
4.8.2 and SENTX latest	AQ33	Dust, Gaseous Emission and LFG including Volatile Organic Compounds (VOCs)	To minimise dust nuisance	SENTX Site	SENTX Contractor	✓	HKAQO and EIAO-TM Annex 4	Implemented
design		• Keeping the main haul road to the waste filling area wet by regular watering;						
4.8.2	AQ34	 Compacting the exposed daily and intermediate covered areas well to avoid fugitive dust emission; 	To minimise dust nuisance	SENTX Site	SENTX Contractor	✓	HKAQO and EIAO-TM Annex 4	Implemented
4.8.2	AQ35	• Limiting the vehicle speed within SENTX site boundary;	To minimise dust nuisance	SENTX Site	SENTX Contractor	✓	HKAQO and EIAO-TM Annex 4	Implemented
4.8.2	AQ36	 Providing vehicle washing bay to avoid vehicles carrying dust to public roads; 	To minimise dust nuisance	SENTX Site	SENTX Contractor	✓	HKAQO and EIAO-TM Annex 4	Implemented
4.8.2	AQ37	• Switching off the engine when the diesel-driven equipment is idling;	To minimise gaseous emissions	SENTX Site	SENTX Contractor	✓ ✓	-	Implemented
4.8.2	AQ38	Maintaining the construction equipment properly to avoid any black smoke	To minimise gaseous	SENTX Site	SENTX Contractor	✓ ✓	-	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	im	easu	men re?	t the		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		emissions;	emissions									
4.8.2	AQ39	Providing sufficient underground landfill gas collection system to capture the landfill gas generated as much as possible; and	To minimise gaseous emissions, including LFG and VOCs	SENTX Site	SENTX Contractor			✓		✓	EIAO-TM Annex 4	Implemented
4.8.2	AQ40	Periodic inspections of the final cover should be undertaken to ensure that the capping layer is in good conditions at all times.	To minimise gaseous emissions, including LFG and VOCs	SENTX Site	SENTX Contractor			✓		✓	EIAO-TM Annex 4	Implemented
4.10.2	AQ41	Monitoring of ambient TSP once every 6 days	Ensure the dust emission from the project meets the dust requirement	shown in	SENTX Contractor		✓	✓	•		HKAQO and EIAO-TM Annex 4	Implemented
4.10.2	AQ42	Monitoring of ambient VOCs, ammonia and H ₂ S, quarterly	Ensure the gaseous emission from the project meets the air quality requirement	At monitoring locations shown in Figure 11.3a	SENTX Contractor			•		√	Odour thresholds or 1% of Occupational Exposure Limit (OEL) as stipulated in the "UK Health and Safety Executive (HSE) EH 40/05 Occupational Exposure Limits", whichever is lower.	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	mea	lem sure	ent th		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
4.10.2 and SENTX latest design	AQ43	Monitoring of parameters for thermal oxidizer, flares and generator in accordance with requirements stated in Tables 3.4a, 3.5a and 3.6a of the EM&A Manual respectively.	Ensure the gaseous emission from the project meets the air quality requirement	At the flares and thermal oxidizer stacks when they are in operation	SENTX Contractor			√	√ (1)	Emission Limits specified in Contract	Implemented
4.10.2	AQ44	To confirm design assumption of ammonia, it is recommended that the ammonia concentration in the flue gas of the thermal oxidiser be monitored during the commissioning stage of the thermal oxidiser. If required, an emission standard will be set for ammonia for the thermal oxidiser based on the monitoring results. If no ammonia is detected in the flue gas during the decommissioning stage, the monitoring of ammonia in the flue gas of the thermal oxidiser could be discontinued.	Ensure the gaseous emission from the project meets the air quality requirement	At the thermal oxidizer stack during commissioning . If ammonia is detected during commissioning stage, the monitoring will continue.	Contractor			✓		Emission Limits determined during commissioning stage	Implemented
4.10.2 and SENTX latest design	AQ45	Odour patrol in accordance with requirements stated in Table 3.7a of the EM&A Manual.	Ensure the odour emission from the project meets the odour requirement	-	SENTX Contractor			✓		EIAO-TM Annex 4	Implemented
4.10.2	AQ46	Monitoring of meteorological station, continuously	Collect site specific	At meteorological	SENTX Contractor		✓	✓	✓	-	Implemented

⁽¹⁾ For LFG flare and LFG generator only.

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
			meteorological data	station shown in <i>Figure 11.3a</i>				
Noise - C	Construction	on Phase						
5.7.1	N1	Adopt good site practice listed below: Only well-maintained plant will be operated on-site and plant should be serviced regularly during the construction program;	To minimise potential construction noise nuisance.	All construction works area	SENTX Contractor	√	Noise Control Ordinance (NCO) and EIAO-TM Annex 5	Implemented
		 Silencers or mufflers on construction equipment should be utilized and will be properly maintained during the construction program; 						
		 Mobile plant, if any, will be sited as far from NSRs as possible; 						
		Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or should be throttled down to a minimum;						
		 Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and 						
		Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site						

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures construction activities.	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When impler measu D C	nent the re? ⁽¹⁾	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
5.8	N2	Weekly noise monitoring	Ensure noise generated from the project meets the criteria	At monitoring locations shown in Figure 6.4a	SENTX Contractor	✓		Noise Control Ordinance (NCO) and EIAO-TM Annex 5	Implemented
Noise - O	peration	Restoration Phase							
5.7.2	N3	Adopt good site practice listed below: • Choose quieter PME;	To minimise potential operational noise nuisance.	Within the SENTX Site	SENTX Contractor		✓	Noise Control Ordinance (NCO) and EIAO-TM Annex 5	Implemented
		• Include noise levels specification when ordering new plant items;						-	Implemented
		• Locate fixed plant items or noise emission points away from the NSRs as far as practicable;						-	Implemented
		Locate noisy machines in completely enclosed plant rooms or buildings; and						-	Implemented
		Develop and implement a regularly scheduled plant maintenance programme so that plant items are properly operated and serviced. The programme should be implemented by properly trained personnel.						-	Implemented
5.8	N4	Weekly noise monitoring	Ensure noise generated from	At monitoring locations	SENTX Contractor		✓	Noise Control Ordinance (NCO) and EIAO-TM	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
			the project meets the criteria	shown in Figure 6.4a			Annex 5	
Water Qu	ality - Co	onstruction Phase						
6.8.1	WQ1	Construction Runoff						
		 Exposed soil areas will be minimised to reduce the contamination of runoff and erosion. 	To minimise	All	SENTX	✓	ProPECC PN 1/94	Implemented
			potential water quality impacts arising from the construction works	construction works area	Contractor		EIAO-TM Annex 6	
6.8.1	WQ2	• Perimeter channels will be constructed in	To minimise	All	SENTX	✓ ✓	ProPECC PN 1/94	Implemented
		advance of site formation works and earthworks and intercepting channels will be provided for example along the edge of excavation.	potential water quality impacts arising from the construction works	construction works area	Contractor		Water Pollution Control Ordinance (WPCO)	
							EIAO-TM Annex 6	
6.8.1	WQ3	Silt removal facilities, channels and	To minimise	All	SENTX	✓	ProPECC PN 1/94	Deficiency of
		manholes will be maintained and the deposited silt and grit should be removed	potential water quality impacts	construction	Contractor		WPCO	mitigation measures but rectified by the
		regularly to ensure they are functioning properly at all times.	arising from the construction works	works area			EIAO-TM Annex 6	Contractor
6.8.1	WQ4	• Temporary covers such as tarpaulin will	To minimise	All	SENTX	✓	ProPECC PN 1/94	Implemented
		generation of high SS runoff.	potential water quality impacts arising from the construction works	construction works area	Contractor		WPCO	

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
6.8.1	WQ5	The surface runoff contained any oil and grease will pass through the oil interceptors.	To minimise potential water quality impacts arising from the construction works	All construction works area	SENTX Contractor	✓	ProPECC PN 1/94 WPCO EIAO-TM Annex 6	Implemented
6.8.1	WQ6	All sewer and drains will be sealed to prevent building debris, soil etc from entering public sewers/drains before commencing any demolition works	To minimise potential water quality impacts arising from the demolition works	Infrastructure area at existing SENT Landfill		✓	ProPECC PN 1/94 WPCO EIAO-TM Annex 6	Not applicable
6.8.1	WQ7	During the excavation works for the twin drainage tunnels, the recycle water for cooling the cutter head of the TBM will be conveyed to the sedimentation tanks for treatment and most of the treated water will be reused, where applicable and as much as possible, in the boring operations.	To minimise potential water quality impacts arising from the tunnel works	Tunnel boring sites	SENTX Contractor	✓	ProPECC PN 1/94 WPCO EIAO-TM Annex 6	Not applicable. Excavation of drainage tunnels is not required in the latest landfill design.
6.8.1	WQ8	The fuel and waste lubricant oil from the on-site maintenance of machinery and equipment will be collected by a licensed chemical waste collector.	To minimise potential water quality impacts arising from improper handling of fuel and oil	SENTX Site	SENTX Contractor	✓	ProPECC PN 1/94 WPCO Waste Disposal Ordinance (WDO)	Implemented
6.8.1	WQ9	Implementation of excavation schedules, lining and covering of excavated stockpiles	To minimise contaminated stormwater runoff from the	All construction works	SENTX Contractor	✓	ProPECC PN 1/94 WPCO EIAO-TM Annex 6	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address SENTX Site	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
6.13	WQ10	Monitoring of surface water quality will be conducted on a regular basis as stated in the EM&A Manual.	To minimise potential water quality impacts on surface water arising from the construction works	SENTX Site	SENTX Contractor	√	WPCO Water-TM	Implemented
6.8.2	WQ11	Sewage Effluents						
		• Sufficient chemical toilets will be provided for the construction workforce.	To minimise potential water quality impacts arising from the sewage effluents	SENTX Site	SENTX Contractor	✓	WPCO	Implemented
6.8.2	WQ12	Untreated sewage will not be allowed to discharge into the surrounding water body.	To minimise potential water quality impacts arising from the sewage effluents	SENTX Site	SENTX Contractor	✓	WPCO WDO	Implemented
6.8.2	WQ13	A licensed waste collector will be employed to clean the chemical toilets on a regular basis.	To minimise potential water quality impacts arising from the sewage effluents	SENTX Site	SENTX Contractor	✓	WPCO WDO	Implemented
Water Qu	ality - O	peration/Restoration and Aftercare Phases						
6.9.1	WQ14	Surface Water Management Inspections of the drainage system, sand	To minimise	SENTX Site	SENTX	✓	WPCO Technical Memorandum	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		traps, settlement ponds and surface water channels will be performed regularly to identify areas necessary for maintenance, cleaning or repair.	potential water quality impacts on surface water arising from the landfill operations.		Contractor		Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Inshore Waters (Water- TM)	
							EIAO-TM Annex 6	
6.9.1	WQ15	Regular maintenance and replacement, if	To minimise	SENTX Site	SENTX	✓	WPCO	Implemented
		conducted to prevent degradation from affecting the performance of the capping system.	potential water quality impacts		Contractor		Water-TM	
			on surface water arising from the landfill operations.				EIAO-TM Annex 6	
6.9.1	WQ16	Monitoring of surface water quality will be conducted on a regular basis as stated in the EM&A Manual.	To minimise potential water quality impacts on surface water arising from the landfill operations.	SENTX Site	SENTX Contractor	✓ ✓	WPCO Water-TM	Implemented
6.9.2 and	WQ17	Groundwater Management						Implemented
SENTX		The groundwater management facilities including the groundwater monitoring wells will be inspected regularly during routine groundwater monitoring programme.	To minimise	SENTX Site	SENTX	✓ ✓	WPCO	
latest design			potential water quality impacts		Contractor		Water-TM	
Ü			on groundwater arising from the landfill operations.				EIAO-TM Annex 6	

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
6.9.2	WQ18	Monitoring of groundwater water quality will be conducted on a regular basis as stated in the EM&A Manual.	To minimise potential water quality impacts on groundwater arising from the landfill operations.	SENTX Site	SENTX Contractor	✓ ✓	WPCO Water-TM EIAO-TM Annex 6	Implemented
SENTX latest design	WQ19	 Sewage All sewage from the operation staff will be diverted to the LTP for treatment or public sewer, if available. 	To ensure proper handling of sewage	SENTX Site	SENTX Contractor	✓ ✓	-	Implemented
6.9.3	WQ20	Leachate Management The leachate pump houses and related ancillary equipment will be inspected regularly and repairs, if necessary.	To minimise potential water quality impacts on surrounding water bodies arising from the landfill operations.	Leachate pump houses and related ancillary equipment	SENTX Contractor	✓ ✓	WPCO Water-TM EIAO-TM Annex 6	Implemented
6.9.3	WQ21	For equipment such as pumps that require routine scheduled maintenance, the maintenance will be performed following manufacturer's recommended frequency.	To minimise potential water quality impacts on surrounding water bodies arising from the landfill operations.	Leachate pumps	SENTX Contractor	√ ✓	WPCO Water-TM	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
6.9.3	WQ22	Preventive maintenance will be implemented so that the possibility for forced shutdown during wet season will be kept to minimal.	To minimise potential water quality impacts on surrounding water bodies arising from the landfill operations.	Leachate treatment plant	SENTX Contractor	✓	√	WPCO Water-TM EIAO-TM Annex 6	Implemented
6.9.3	WQ23	• Emergency procedures or a contingency plan will be established when the LTP is malfunctioned.	To minimise potential water quality impacts on surrounding water bodies arising from the landfill operations.	Leachate treatment plant	SENTX Contractor	✓	√	WPCO Water-TM EIAO-TM Annex 6	Implemented
6.9.3 and SENTX latest design	WQ24	• There will be sufficient redundancy in the system to handle the leachate flow even if one treatment train is down for maintenance. The leachate may be required to temporarily store within the landfill if the leachate storage lagoon are full and leachate cannot be transported to the LTP for treatment.	To minimise potential water quality impacts on surrounding water bodies arising from the landfill operations.	Leachate treatment plant	SENTX Contractor	✓	√	WPCO Water-TM EIAO-TM Annex 6	Implemented
6.13	WQ25	Monitor the quality of effluent discharged from the LTP	To ensure discharge quality comply with WPCO requirement	Leachate treatment plant discharge point	SENTX Contractor	√	✓	WPCO Water-TM	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When imple measu D C	ment th		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
6.10.1	WQ26	Potential Leakage of Leachate • Regular groundwater quality monitoring will be carried out to monitor the performance of the leachate containment system.	To minimise potential water quality impacts on surrounding water bodies arising from the landfill operations.	SENTX Site	SENTX Contractor		√	√	WPCO Water-TM	Implemented
6.10.1	WQ27	 Maintenance and replacement of the capping system should be carried out, if necessary, to prevent control infiltration and leachate seepage from any damaged cap. 	To minimise potential water quality impacts on surrounding water bodies arising from the leachate leakage.	SENTX Site	SENTX Contractor		✓	√	WPCO Water-TM EIAO-TM Annex 6	Implemented
6.10.1	WQ28	Maintaining control of the leachate level through extraction	To minimise potential water quality impacts on surrounding water bodies arising from surface breakout of leachate.	SENTX Site	SENTX Contractor		√	✓	WPCO Water-TM EIAO-TM Annex 6	Implemented
Waste Ma	anagemen	t - Construction Phase								
7.6.1	WM1	All the necessary waste disposal permits are obtained prior to the commencement of construction work.	To ensure compliance with relevant statutory	Before construction works	SENTX Contractor	✓ ✓			WDO	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
			requirements	commence				
7.6.1	WM2	Management of Waste Disposal						
		The construction contractor will open a	To ensure that	SENTX Site	SENTX	✓	WDO	Implemented
		billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will required a	•		Contractor		Waste Disposal (Charges for Disposal of Construction Waste) Regulation;	
		valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste					Works Bureau Technical Circular No.31/2004; and	
		producer. A trip-ticket system will also be established to monitor the disposal of construction waste at the SENT Landfill and to control fly-tipping. The trip-ticket system will be included as one of the contractual requirements and implemented by the contractor.					Annex 5 and Annex 6 of Appendix G of ETWBTC No. 19/2005)	
		A recording system for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established.						
7.6.1	WM3	Measures for the Reduction of Construction Waste Generation						
		Inert and non-inert construction waste will be segregated and stored in different containers or skips to facilitate reuse or recycling of the inert waste and proper disposal of the non-	To reduce construction waste generation	SENTX Site	SENTX Contractor	✓	WDO EIAO-TM Annex 7	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		inert construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.						
7.6.1	WM4	Chemical Waste						
		The construction contractor will register as a chemical waste producer with the EPD. Chemical waste will be handled in accordance with the <i>Code of Practice on the Packaging, Handling and Storage of Chemical Wastes</i> .	To ensure proper handling of chemical waste	SENTX Site	SENTX Contractor	✓	WDO Code of Practice on the Packaging, Handling and Storage of Chemical Wastes	Deficiency of mitigation measures but rectified by the Contractor
7.6.1	WM5	<u>Sewage</u>						
		An adequate number of portable toilets will be provided at the site to ensure that sewage from site staff is properly collected. The portable toilets will be desludged and maintained regularly by a specialist contractor.	To ensure proper handling of sewage	SENTX Site	SENTX Contractor	✓	WDO EIAO-TM Annex 7	Implemented
7.6.1 and	WM6	General Refuse						
SENTX latest		General refuse will be stored in enclosed bins		SENTX Site	SENTX	✓	WDO	Deficiency of
design		separately from construction and chemical wastes. The general refuse will be delivered to a transfer station or other landfill, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	handling of general refuse		Contractor		EIAO-TM Annex 7	mitigation measures but rectified by the Contractor
		Recycling bins will be provided at strategic locations to facilitate recovery of aluminium						

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		can and waste paper from the SENTX Site. Materials recovered will be sold for recycling.						
7.6.1	WM7	Staff Training						
		At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	To ensure that adverse environmental impacts are prevented	SENTX Site	SENTX Contractor	✓		Implemented
7.8	WM8	Environmental Monitoring & Audit Requirements						
		Weekly audits of the waste management practices will be carried out during the construction phase. The audits examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	To ensure that adverse environmental impacts are prevented	SENTX Site	SENTX Contractor	~	WDO	Implemented
Waste Ma	ınagemen	t – Operation/Restoration Phase						
7.6.2 and SENTX latest design	WM9	Sludge In case off-site disposal is required, the Contractor will ensure that sludge generated from the LTP will be delivered in closed container to other waste disposal facility e.g. other landfills or a sludge treatment facility, for proper disposal on a daily basis.	To ensure proper handling of sludge	SENTX Site	SENTX Contractor	✓	WDO EIAO-TM Annex 7	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
7.6.2	WM10	Chemical Waste						Implemented
		The construction contractor will register as a	To ensure proper	SENTX Site	SENTX	✓	WDO	
		chemical waste producer with the EPD. Chemical waste will be handled in	handling of chemical waste		Contractor		EIAO-TM Annex 7	
		accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes.					Code of Practice on the Packaging, Handling and Storage of Chemical Wastes	
7.6.2	WM11	Sewage						Moved to mitigation
		All sewage from the operation staff will be	To ensure proper	SENTX Site	SENTX	✓	WDO	measure under water quality
		diverted to the LTP for treatment or public sewer, if available.	handling of sewage		Contractor		EIAO-TM Annex 7	WQ19. It is a measure for water quality rather than waste management.
7.6.2 and	WM12	General Refuse						Implemented
SENTX latest		General refuse will be stored in enclosed bins		SENTX Site	SENTX	✓	WDO	
design		and disposed of at other landfills or transfer station on a daily basis to reduce odour, pest and litter impacts.	handling of general refuse		Contractor		EIAO-TM Annex 7	
		Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the SENTX Site. Materials recovered will be sold for recycling.						
Landfill G	Gas Hazaı	rds - Design and Construction Phase						
8.6.2 and	LFG1	Precautionary measures to be adopted by the	To protect	All	SENTX	✓	Paragraphs 8.3 to 8.49 of	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
SENTX latest design		contractors at the Project site and the adjacent development site within the landfill consultation zone are outlined in Paragraphs	workers from landfill gas risk	construction works area	Contractor		EPD's Landfill Gas Hazards Assessment Guidance Note	
		8.3 to 8.49 of EPD's Landfill Gas Hazard Assessment Guidance Notes (the Guidance Note). Those precautionary measures applicable to the SENTX will be confirmed in the detailed Qualitative Landfill Gas Hazard Assessment to be submitted by the contractor.					EIAO-TM Annex 7	
8.6.2	LFG2	Monitoring will be undertaken when construction works are carried out in confined space within the consultation zone with reference to the monitoring requirements and procedures specified in Paragraphs 8.23 to 8.28 of EPD's <i>Guidance Note</i> will be followed.	To protect workers from landfill gas risk	Confined space within the construction works area	SENTX Contractor	✓		Implemented
		In the event of the trigger levels being exceeded, it is recommended that a person, such as the Safety Officer, is nominated, with deputies, to be responsible for dealing with any emergency which may occur due to landfill gas. In an emergency situation, the nominated person, or his deputies, shall have the necessary authority and shall ensure that the confined space is evacuated and the necessary works implemented for reducing the concentrations of gas. The appropriate organisations shall be contact.						
8.6.3	LFG4	Implementation of engineering measures according to Contract Specification	To protect workers from	SENTX Site	SENTX Contractor	✓ ✓ ✓	EIAO-TM Annex 7	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	imp mea	en to Jemen Isure? (What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		requirements. These measures will include the placement of liner and installation of landfill gas management system to contain, manage and control landfill gas.	landfill gas risk							
8.6.3	LFG5	Engineering measures to significant engineering measures will be required in the design of the SENTX to protect the staff working in the infrastructure area. These measures include a combination of passive and active systems (examples are recommended in EPD's <i>Guidance Notes</i>). Landfill gas monitoring boreholes will be installed at the edge of the waste slope between the waste and the new infrastructure area to monitor the migration of landfill gas, if any.	To protect workers from landfill gas risk	Infrastructure Area	SENTX Contractor	✓	✓		EPD's Landfill Gas Hazards Assessment Guidance Note EIAO-TM Annex 7	Implemented
Landfill (Phases	Gas Haza	rds - Operation, Restoration and Aftercare								
8.6.4	LFG7	To train and ensure staff to take appropriate precautions at all times when entering enclosed spaces or plant rooms. Undertake regular monitoring of landfill gas at the perimeter boreholes to detect if there are any signs of off-site landfill gas migration. Prepare and implement emergency plan in case off-site landfill gas migration is detected. A permanent gas monitoring system with alarm will be installed and operated in all occupied on-site buildings.	To protect workers from landfill gas risk	SENTX Site	SENTX Contractor		√	✓	Landfill Gas Hazards Assessment Guidance Note	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
8.7 and SENTX latest design	LFG8	Environmental Monitoring & Audit Requirements Undertake regular monitoring of landfill gas within the SENTX and along the SENTX boundary as required by the Contract Specification.	To protect workers from landfill gas risk	Within the SENTX and along the SENTX boundary	SENTX Contractor	√ ✓	Landfill Gas Hazards Assessment Guidance Note	Implemented
Ecology -	Construc	tion Phase						
9.10.2	EC1	Measures to control construction runoff:	To minimise potential water quality impacts affecting ecological resources	All construction works area	SENTX Contractor	~	EIAO-TM Annex 16 ProPECC PN 1/94 Water Pollution Control Ordinance (WPCO) EIAO-TM Annex 6	Implemented
		 To prevent stormwater runoff from washing across exposed soil surfaces, perimeter channels will be constructed in advance of site formation works and earthworks and intercepting channels will be provided for example along the edge of excavation; 					-	impiemented
		 Silt removal facilities, channels and manholes will be maintained and the deposited silt and grit will be removed regularly to ensure they are functioning properly at all times; 					-	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		 Temporary covers such as tarpaulin will also be provided to minimise the generation of high suspended solids runoff; 					-	Implemented
		The surface runoff contained any oil and grease will pass through the oil interceptors; and,					-	Implemented
		Control measures, including implementation of excavation schedules, lining and covering of excavated stockpiles will be implemented to minimise contaminated stormwater run-off from the SENTX site.					-	Implemented
9.10.2	EC2	Good Construction Practice:						
and SENTX latest design		• Fences along the boundary of the SENTX Site will be erected before the commencement of works to prevent vehicle movements, and encroachment of personnel, onto adjacent areas.	To minimise potential ecological impacts arising from the Project	SENTX Site	SENTX Contractor	✓	EIAO-TM Annex 16	Implemented
		• The work site boundaries will be regularly checked to ensure that they are not breached and that damage does not occur to surrounding areas.						
Ecology -	Operatio	n, Restoration and Aftercare Phases						
9.10.2	EC3	<u>Measures for Controlling Leakage of Landfill</u> <u>Leachate</u>						Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	im _] me	asu	men re?	nt the		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
9.10.2	EC4	Leachate will be contained within the SENTX Site by the proposed impermeable leachate containment system and collected by the installation of drainage system to prevent potential migration of leachate to habitats in the vicinity. Measures for Controlling Migration of	To minimise potential water quality impact affecting the ecological resources	SENTX Site	SENTX Contractor			~	•	✓	EIAO-TM Annex 16 WPCO Water-TM EIAO-TM Annex 6	Implemented
		Landfill Gas Disturbance to habitat in the vicinity and associated wildlife due to migration of landfill gas will be prevented by proper management of the landfill gas generated from the SENTX. Ignition fires will be prohibited to occur within the boundary of the SENTX Site. Surface emission and offsite migration of landfill gas will be regularly monitored.	To minimise potential landfill gas migration affecting ecological resources	SENTX Site	SENTX Contractor			~		✓	EIAO-TM Annex 16	r
9.10.3 and SENTX latest design	EC5	 The following compensation planting is recommended as the mitigation measures for the habitat affected due to the SENTX: Provision of 6 ha of mixed woodland planting to compensate the loss of shrubland; and Provision of a mosaic of grassland and shrubland in the remaining areas of the SENTX Site. Compensatory planting and restoration of the SENTX can be implemented progressively according to the filling plan of SENTX. 	Compensation of habitat loss due to the Project	SENTX Site	SENTX Contractor			~	,	√	EIAO-TM Annex 16	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	im me	ple easi	ure	ent th		What requirements or standards for the measure to achieve?	Implementation Status and Remarks
9.10.3	EC6	The mixture of grassland, shrubland and woodland habitats are recommended to diversify the habitats for supporting various wildlife in particular butterflies, birds and herpetofauna and blend into the existing undisturbed ecological environment.	To diversify habitats	SENTX Site	SENTX Contractor				✓	✓	EIAO-TM Annex 16	Implemented
9.10.3	EC7	Indigenous plant species of shallow root system, softwood in nature and adaptive to sea shore habitat are recommended to be used in the restoration plan, which can establish well in coastal area with exposure to strong wind and salt spray, with sand soil base. Taking consideration of the relative poor substrate and the difficulties of establishment of some native trees in Hong Kong, it is recommended to include approximately 20% of non-native tree species in the compensatory woodland. The non-native tree species can serve as a nurse species to facilitate the establishment of the native tree species, especially the shading, and it can be replaced by established native tree species progressively. Plant species can also make reference to food plants of butterfly species (in particularly butterfly species of conservation interests recorded within the CWBCP).	To enhance ecological value of the habitats	SENTX Site	SENTX Contractor				•	✓	EIAO-TM Annex 16	Implemented
9.10.3	EC8	It is also recommended that a trial nursery for native plant species be set up to fine tone the planting matrix and management intensity of the recommended indigenous tree species for	To select the most suitable indigenous tree species for the	SENTX Site	SENTX Contractor	✓			✓	√	EIAO-TM Annex 16	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		the restoration of the SENTX. It should be noted that native shrubs and tree species had been used for restoration of the existing SENT Landfill, native plant species that could not successfully be established on the existing SENT Landfill should be reviewed before the preparation of the compensatory planting list. Special care and intensive management of native plant should be implemented in order to ensure proper establishment of the native plants.	SENTX					
9.12.1	EC9	Environmental Monitoring & Audit Requirements The implementation of the ecological mitigation measures should be checked as part of the environmental monitoring and audit procedures during the construction period.	To ensure that adverse ecological impacts are prevented	SENTX	SENTX Contractor	✓ ✓ ✓	EIAO-TM Annex 16	Implemented
Landscap	e and Vis	ual - Construction Phase						
10.6.5	LV1	CM1 - The construction area and area allowed for the contractor's office, leachate treatment plant and laboratory areas will be minimised to a practical minimum, to avoid impacts on adjacent landscape.	To minimise the landscape and visual impacts	SENTX Site	SENTX Contractor	✓	EIAO-TM Annex 18 and ETWBC 3/2006	Implemented
10.6.5	LV2	CM2 - Topsoil, where identified, will be stripped and stored for re-use in the construction of the soft landscape works, where practical. The Contract Specification	To minimise the landscape and visual impacts	All construction works area	SENTX Contractor	✓	EIAO-TM Annex 18	Not applicable

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		will include storage and reuse of topsoil as appropriate.						
10.6.5	LV3	CM3 - All existing trees at the edges of the landfill will be carefully protected during construction. Detailed Tree Protection Specification will be provided in the Contract Specification. Under this Specification, the Contractor will be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in Contractor's works areas.	To minimise the landscape and visual impacts	Potential impacted area	SENTX Contractor		EIAO-TM Annex 18 and ETWBC 3/2006	Not applicable
10.6.5	LV4	CM4 - Trees unavoidably affected by the works will be transplanted, where necessary and practical. A detailed Tree Transplanting Specification will be provided in the Contract Specification, if applicable. Sufficient time for necessary tree root and crown preparation periods will be allowed in the project programme.	To minimise the landscape and visual impacts	Potential impacted area	SENTX Contractor	✓ ✓	EIAO-TM Annex 18 and ETWBC 3/2006	Implemented
10.6.5 and SENTX latest design	LV5	CM5 - Within 3 months of taking possession of the SENTX Site, the Contractor will plant advance screen planting of native species at Light Standard size at 1.5m centres along the High Junk Peak Trail so as to screen views of the Works from the trail. Tree planting locations will be agreed with AFCD. Works will be completed within 9 months of taking possession of the SENTX Site.	To minimise the landscape and visual impacts	At High Junk Peak Hiking Trail	SENTX Contractor	✓	EIAO-TM Annex 18	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	im	hen to plement the easure? (1) C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
10.6.5	LV6	CM6 - The Contractor's office, leachate treatment plant and laboratory will be given an aesthetic treatment in earth tones to reduce their visual impact and albedo and blend them into the surrounding landscape.	To minimise the landscape and visual impacts	Infrastructure area	SENTX Contractor	✓	√	EIAO-TM Annex 18	Implemented
10.6.5	LV7	CM7 - The Contractor's office, leachate treatment plant and laboratory will be surrounded by a minimum of 5m wide and 0.75m high earth bund on the west and south sides planted with a dense screen of tree and shrub vegetation. Additional tree planting will be provided in unused spaces with thin infrastructure site, along access roads and in and around car parks. This will be supplemented with shrub planting, where appropriate.	To minimise the landscape and visual impacts	Infrastructure area	SENTX Contractor	√	✓	EIAO-TM Annex 18 and ETWBC 7/2002	Not applicable
10.6.5	LV8	CM8 - Planting trials will be carried out in an on-site nursery prior to implementation of the first phase of restoration to establish the best planting matrix and management intensity of the recommended plant materials for the restoration.		SENTX Site	SENTX Contractor		✓	EIAO-TM Annex 18	Implemented
11.4.1 and SENTX latest design	LV9	During the preparation of the detailed landscape design plan, the design submission will be audited against the recommendation proposed in the <i>ER Report</i> by the Registered Landscape Architect from the ET.	To ensure the implementation of mitigation measures proposed in this EIA Report	SENTX Site	SENTX Contractor/ET	✓	✓	EIAO-TM Annex 18	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Recommended the Measures implement the im		When to implement the measure? (1) D C O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks	
Landscap	e and Vis	ual - Operation/Restoration Phase						
10.6.5 and SENTX latest design	LV10	OM1 - Landfill materials will be covered with general fill material or tarpaulin sheet on a daily basis to reduce visual impact.	To minimise the landscape and visual impacts	Tipping area	SENTX Contractor	✓	EIAO-TM Annex 18	Implemented
10.6.5 and SENTX latest design	LV11	OM2 - Filling and restoration will be phased during the course of operations in a minimum of 4 phases, the restoration of each phase to commence immediately on the completion of filling in that phase.	To minimise the landscape and visual impacts	Tipping area	SENTX Contractor	✓	EIAO-TM Annex 18	Implemented
10.6.5	LV12	OM3 - Catch fences will be erected at the perimeter of the waste boundary, to ensure that all waste stays within the site and is not blown into surrounding areas.	To minimise the landscape and visual impacts	Tipping area	SENTX Contractor	✓	EIAO-TM Annex 18	Implemented
10.6.5	LV13	OM4 - All night-time lighting will be reduced to a practical minimum both in terms of number of units and lux level and will be hooded and directional.	To minimise the landscape and visual impacts	Tipping area	SENTX Contractor	✓	EIAO-TM Annex 18	Implemented
and SENTX latest design	LV14	The condition of the restoration plantation will be audited at monthly intervals by a Registered Landscape Architect from the ET.	To check the restoration plantation	SENTX Site	SENTX Contractor/ET	✓	EIAO-TM Annex 18	Implemented

Annex C

Monitoring Schedule for This Reporting Period

South East New Territories (SENT) Landfill Extension EM&A Impact Monitoring Schedule during Operation/ Restoration Phase

<u>July 2022</u>

Sun	Mon	Tue	Wed	Thu	Fri	Sat
					Leachate Monitoring	Leachate Monitoring
3 Leachate Monitoring	4 Groundwater Monitoring	5 Dust Monitoring	6 Noise Monitoring	7 Leachate Monitoring	8 Additional Surface Water Monitoring	Leachate Monitoring
	Leachate Monitoring	Groundwater Monitoring	Leachate Monitoring		Leachate Monitoring	
		Leachate Monitoring				
Leachate Monitoring	11 Dust Monitoring	Perimeter LFG Monitoring	Service Void LFG Monitoring	14 Leachate Monitoring	15 Additional Surface Water Monitoring	16 Leachate Monitoring
	Leachate Monitoring	Stack Monitoring	Leachate Monitoring		Leachate Monitoring	
		Leachate Monitoring				
		Noise Monitoring				
17 Dust Monitoring	18 Stack Monitoring	19 Leachate Monitoring	20 Leachate Monitoring	21 Leachate Monitoring	22 Leachate Monitoring	23 Dust Monitoring
Leachate Monitoring	Noise Monitoring				Odour Monitoring	Leachate Monitoring
	Leachate Monitoring					
24 Leachate Monitoring	25 Noise Monitoring	26 Leachate Monitoring	27 Leachate Monitoring	28 Leachate Monitoring	29 Dust Monitoring	30 Leachate Monitoring
	Surface Water Monitoring				Leachate Monitoring	
	Leachate Monitoring					
31						
Leachate Monitoring						

Air Quality

Calibration Certificates for Dust Monitoring Equipment

Location ID: AM1 Date of Calibration: 19-May-22
Name and Model: TISCH HVS Model TE-5170 Next Calibration Date: 19-Jul-22

Operator: Dixon Chan

CONDITIONS

Sea Level Pressure (hPa)
Temperature (°C)

1011.9
25.8

Corrected Pressure (mm Hg)
Temperature (K)

758.925 299

CALIBRATION ORIFICE

Make->	TISCH
Model->	5025A
Serial # ->	1612

Qstd Slope -> Qstd Intercept ->

1.99838

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	5.70	5.70	11.4	1.691	60	59.80	Slope = 33.7639
13	4.50	4.50	9.0	1.503	54	53.82	Intercept = 2.9958
10	3.50	3.50	7.0	1.326	48	47.84	Corr. coeff. = 0.9995
7	2.30	2.30	4.6	1.076	40	39.86	
5	1.30	1.30	2.6	0.810	30	29.90	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

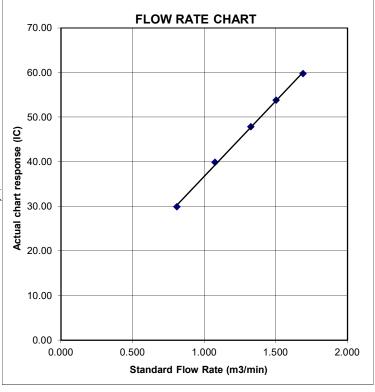

Location ID: AM2 Date of Calibration: 19-May-22
Name and Model: TISCH HVS Model TE-5170 Next Calibration Date: 19-Jul-22

Operator: Dixon Chan

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C)

1011.9
25.8

Corrected Pressure (mm Hg)
Temperature (K)

758.925 299

CALIBRATION ORIFICE

Make->	TISCH
Model->	5025A
Serial # ->	1612

Qstd Slope -> Qstd Intercept ->

1.99838

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.40	6.40	12.8	1.791	52	51.82	Slope = 31.8110
13	5.10	5.10	10.2	1.599	45	44.85	Intercept = -5.2670
10	3.90	3.90	7.8	1.399	40	39.86	Corr. coeff. = 0.9987
7	2.50	2.50	5.0	1.121	31	30.90	
5	1.50	1.50	3.0	0.869	22	21.93	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

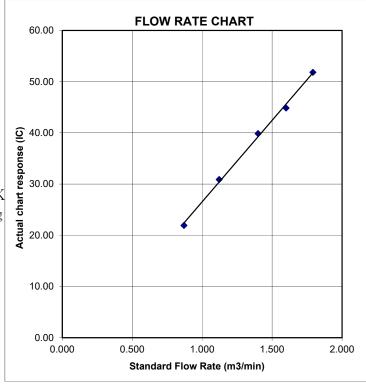

Location ID: AM3 Date of Calibration: 19-May-22
Name and Model: TISCH HVS Model TE-5170 Next Calibration Date: 19-Jul-22

Operator: Dixon Chan

CONDITIONS

Sea Level Pressure (hPa)
Temperature (°C)

1011.9 25.8

Corrected Pressure (mm Hg)
Temperature (K)

758.925

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1612

Qstd Slope -> Qstd Intercept ->

1.99838 -0.00903

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	5.40	5.40	10.8	1.646	56	55.81	Slope = 42.8543
13	4.00	4.00	8.0	1.417	48	47.84	Intercept = -14.5250
10	3.60	3.60	7.2	1.344	42	41.86	Corr. coeff. = 0.9965
7	2.40	2.40	4.8	1.099	32	31.89	
5	1.40	1.40	2.8	0.840	22	21.93	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Ostd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

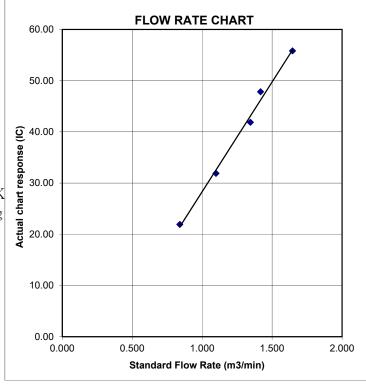

Location ID: AM4 Date of Calibration: 19-May-22
Name and Model: TISCH HVS Model TE-5170 Next Calibration Date: 19-Jul-22

Operator: Dixon Chan

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C)

1011.9
25.8

Corrected Pressure (mm Hg)
Temperature (K)

758.925 299

CALIBRATION ORIFICE

Make->	TISCH
Model->	5025A
Serial # ->	1612

Qstd Slope -> Qstd Intercept ->

1.99838 -0.00903

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.20	6.20	12.4	1.763	54	53.82	Slope = 28.3766
13	4.90	4.90	9.8	1.568	48	47.84	Intercept = 3.6780
10	3.80	3.80	7.6	1.381	43	42.85	Corr. coeff. = 0.9991
7	2.30	2.30	4.6	1.076	35	34.88	
5	1.50	1.50	3.0	0.869	28	27.91	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

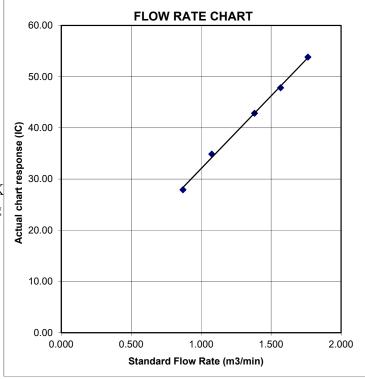

Location ID: AM1 Date of Calibration: 18-Jul-22
Name and Model: TISCH HVS Model TE-5170 Next Calibration Date: 18-Sep-22

Operator: Dixon Chan

CONDITIONS

Sea Level Pressure (hPa)
Temperature (°C)

1004.9
30.4

Corrected Pressure (mm Hg)
Temperature (K)

753.675 303

CALIBRATION ORIFICE

Make->	TISCH
Model->	5025A
Serial # ->	1612

Qstd Slope -> Qstd Intercept ->

1.99838

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	5.70	5.70	11.4	1.672	59	57.71	Slope = 42.3021
13	4.40	4.40	8.8	1.470	52	50.86	Intercept = -12.4750
10	3.50	3.50	7.0	1.311	43	42.06	Corr. coeff. = 0.9978
7	2.30	2.30	4.6	1.064	34	33.26	
5	1.50	1.50	3.0	0.860	24	23.47	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

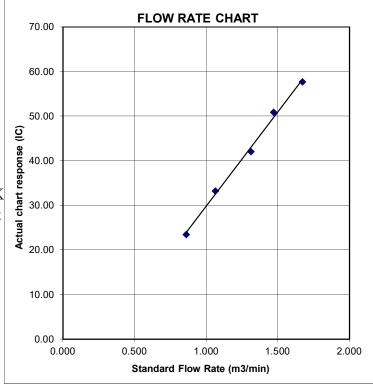

Location ID: AM2 Date of Calibration: 18-Jul-22
Name and Model: TISCH HVS Model TE-5170 Next Calibration Date: 18-Sep-22

Operator: Dixon Chan

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1004.9 30.4

Corrected Pressure (mm Hg)
Temperature (K)

753.675 303

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1612

Qstd Slope -> Qstd Intercept ->

1.99838 -0.00903

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	6.00	6.00	12.0	1.715	52	50.86	Slope = 30.9016
13	4.80	4.80	9.6	1.535	46	44.99	Intercept = -2.5771
10	3.70	3.70	7.4	1.348	39	38.15	Corr. coeff. = 0.9988
7	2.30	2.30	4.6	1.064	31	30.32	
5	1.30	1.30	2.6	0.801	23	22.50	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Ostd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

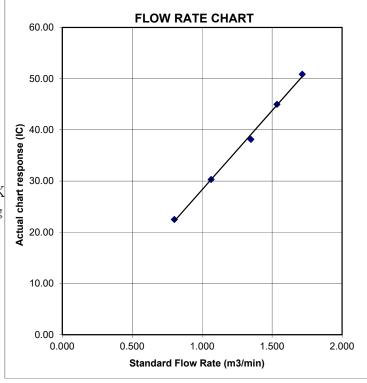

Location ID: AM3 Date of Calibration: 18-Jul-22
Name and Model: TISCH HVS Model TE-5170 Next Calibration Date: 18-Sep-22

Operator: Dixon Chan

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1004.9 30.4

Corrected Pressure (mm Hg)
Temperature (K)

753.675 303

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1612

Qstd Slope -> Qstd Intercept ->

1.99838 -0.00903

CALIBRATION

							-
Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	5.70	5.70	11.4	1.672	58	56.73	Slope = 36.7741
13	4.50	4.50	9.0	1.486	52	50.86	Intercept = -4.2418
10	3.40	3.40	6.8	1.292	44	43.04	Corr. coeff. = 0.9978
7	2.20	2.20	4.4	1.040	36	35.21	
5	1.40	1.40	2.8	0.831	26	25.43	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Ostd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

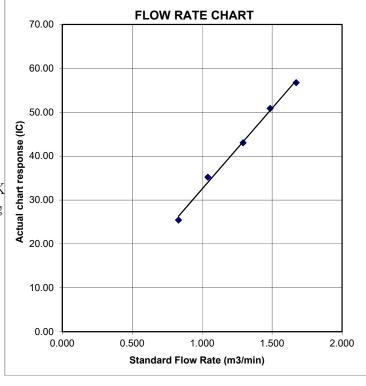

Location ID: AM4 Date of Calibration: 18-Jul-22
Name and Model: TISCH HVS Model TE-5170 Next Calibration Date: 18-Sep-22

Operator: Dixon Chan

CONDITIONS

Sea Level Pressure (hPa) Temperature (°C) 1004.9 30.4

Corrected Pressure (mm Hg)
Temperature (K)

753.675

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1612

Qstd Slope -> Qstd Intercept ->

1.99838

CALIBRATION

Plate	H20 (L)	H2O (R)	H20	Qstd	I	IC	LINEAR
No.	(in)	(in)	(in)	(m3/min)	(chart)	corrected	REGRESSION
18	5.90	5.90	11.8	1.701	53	51.84	Slope = 30.9549
13	4.60	4.60	9.2	1.502	48	46.95	Intercept = -0.3923
10	3.70	3.70	7.4	1.348	42	41.08	Corr. coeff. = 0.9989
7	2.30	2.30	4.6	1.064	33	32.28	
5	1.40	1.40	2.8	0.831	26	25.43	

Calculations:

Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart respones

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

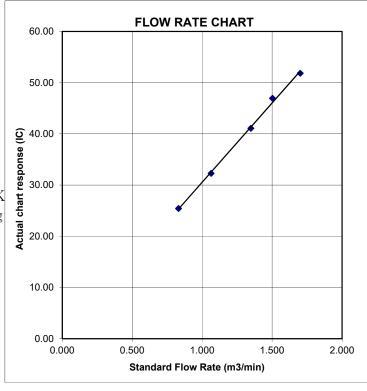

24-hour TSP Monitoring Results

Table D2.1 24-hour TSP Monitoring Results at AM1

Start Date	Start Time	Finish Date	Finish Time	Weather	24-hour TSP (μg/m3)
5 Jul 22	9:00	6 Jul 22	8:21	Fine	42
11 Jul 22	9:00	12 Jul 22	8:47	Fine	52
17 Jul 22	9:00	18 Jul 22	8:41	Fine	39
23 Jul 22	9:00	24 Jul 22	9:09	Sunny	58
29 Jul 22	9:00	30 Jul 22	9:12	Sunny	156
				Average	69
				Min	39
				Max	156

Figure D2.1 Graphical Presentation for 24-hr TSP Monitoring at AM1

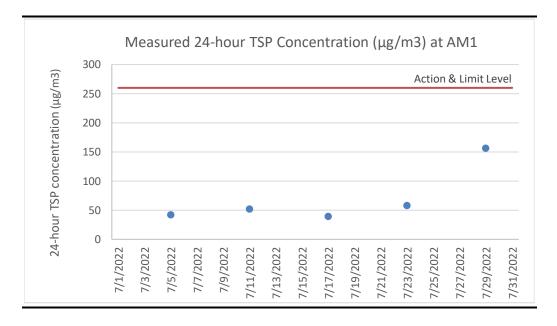


Table D2.2 24-hour TSP Monitoring Results at AM2

Start Date	Start Time	Finish Date	Finish Time	Weather	24-hour TSP (µg/m3)
5 Jul 22	9:00	6 Jul 22	9:03	Fine	43
11 Jul 22	9:00	12 Jul 22	9:01	Fine	96
17 Jul 22	9:00	18 Jul 22	9:00	Fine	64
23 Jul 22	9:00	24 Jul 22	8:59	Sunny	118
29 Jul 22	9:00	30 Jul 22	9:00	Sunny	312
				Average	127
				Min	43
				Max	312

Figure D2.2 Graphical Presentation for 24-hr TSP Monitoring at AM2

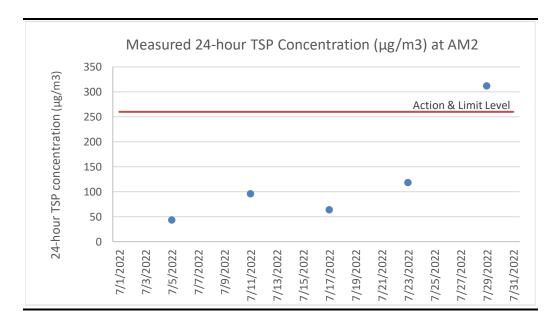


Table D2.3 24-hour TSP Monitoring Results at AM3

Start Date	Start Time	Finish Date	Finish Time	Weather	24-hour TSP (μg/m3)
5 Jul 22	9:00	6 Jul 22	8:43	Fine	56
11 Jul 22	9:00	12 Jul 22	8:14	Fine	93
17 Jul 22	9:00	18 Jul 22	9:32	Fine	72
23 Jul 22	9:00	24 Jul 22	8:33	Sunny	132
29 Jul 22	9:00	30 Jul 22	9:34	Sunny	241
				Average	119
				Min	56
				Max	241

Figure D2.3 Graphical Presentation for 24-hr TSP Monitoring at AM3


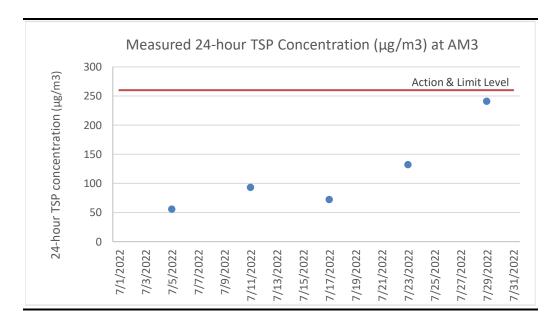


Table D2.4 24-hour TSP Monitoring Results at AM4

Start Date	Start Time	Finish Date	Finish Time	Weather	24-hour TSP (μg/m3)
5 Jul 22	9:00	6 Jul 22	8:36	Fine	72
11 Jul 22	9:00	12 Jul 22	8:33	Fine	42
17 Jul 22	9:00	18 Jul 22	9:11	Fine	98
23 Jul 22	9:00	24 Jul 22	9:15	Sunny	144
29 Jul 22	9:00	30 Jul 22	9:17	Sunny	364
				Average	144
				Min	42
				Max	364

Figure D2.4 Graphical Presentation for 24-hr TSP Monitoring at AM4

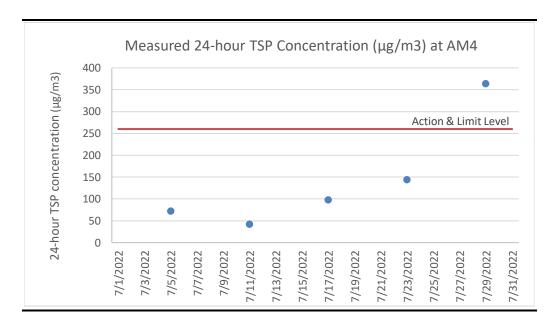

Event and Action Plan for Dust Monitoring

Annex D3 Event and Action Plan for Air Quality Monitoring During Operation/Restoration Phase


		Action	
Event	ET	IEC	Contractor
Exceedance of Action/Limit Level for dust monitoring	 Identify the source(s) and investigate the cause(s) of exceedance Prepare the Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures Ensure remedial measures are properly implemented Assess effectiveness of Contractor's remedial measures and keep the Project Proponent and IEC informed of the results Repeat measurement to confirm finding if exceedance is due to the Project Increase monitoring frequency to daily and continue until the monitoring results reduce to below action level 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Check Contractor's working methods Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Take immediate action to avoid further exceedance Submit proposals for remedial measures to IEC Implement the agreed proposals Amend proposal if appropriate
Exceedance of Action Level for odour	 Identify source(s) and investigate the cause(s) of exceedance or complaint Prepare the odour complaint form or the Notification of Exceedance within 24 hours Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures Ensure remedial measures are properly implemented Increase monitoring frequency to daily until odour not being detected for three consecutive da 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Check Contractor's working methods Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Rectify any unacceptable practice Amend working methods as required Implement amended working methods, if necessary


Action				
Event	ET	IEC	Contractor	
Exceedance of Limit Level for odour	 Identify source(s) and investigate the cause(s) of exceedance or complaint Prepare the odour complaint form or the Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures Ensure remedial measures are properly implemented Assess effectiveness of Contractor's remedial measures and keep the Project Proponent and IEC informed of the results 	 Verify the Notification of Exceedance Check with Contractor on the operating activities and implementation of odour mitigation measures Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Rectify any unacceptable practice Submit proposals for remedial measures to IEC within 3 working days of notification Implement the agreed proposal or amend working methods as required Resubmit proposals if problem still not under control 	
Exceedance of Limit Level for ambient VOCs, ammonia and H ₂ S at the monitoring locations	 Identify the source(s) and investigate the cause(s) of exceedance Prepare the Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures Ensure remedial measures are properly implemented Assess effectiveness of Contractor's remedial measures and keep the Project Proponent and IEC informed of the results Repeat measurement to confirm finding if exceedance is due to the Project Increase monitoring frequency to monthly and continue until the monitoring results reduce to below limit level 	 Check with Contractor on the operating activities and implementation of landfill gas control measures 	 Rectify any unacceptable practice Amend working methods as required Implement amended working methods, if necessary 	


Action				
Event	ET	IEC	Contractor	
Exceedance of Limit Level of stack emission of the thermal oxidizer, flares and generator	 Identify source(s) and investigate the cause(s) of exceedance Prepare the Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures Ensure remedial measures are properly implemented Assess effectiveness of Contractor's remedial measures and keep the Project Proponent and IEC informed of the results Repeat measurement to confirm finding if exceedance is due to the Project Increase monitoring frequency to monthly when there are two consecutive exceedances and continue until the monitoring results reduce to below limit level 	 Verify the Notification of Exceedance Check with Contractor on the operating performance of the stack Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Rectify any unacceptable performance Amend design as required Implement amended design, if necessary 	


Meteorological Data


Annex D4 Meteorological Data

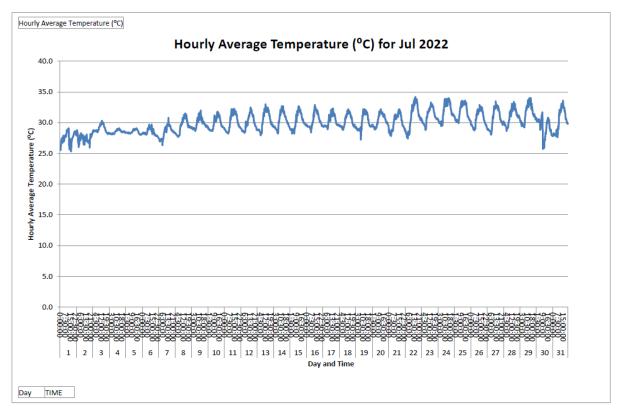


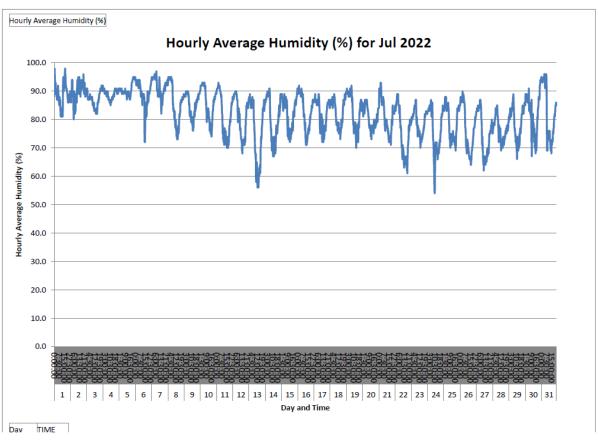


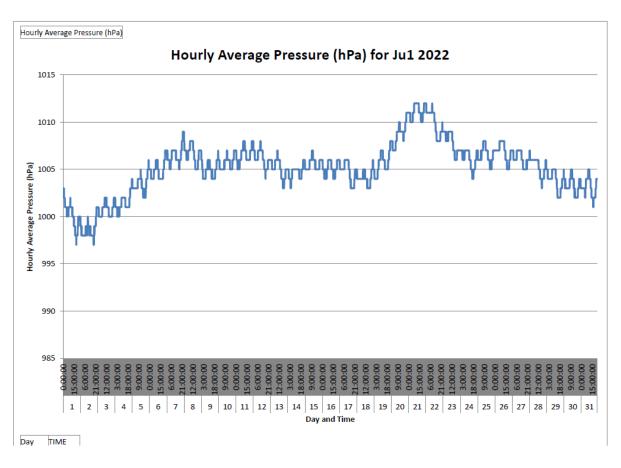

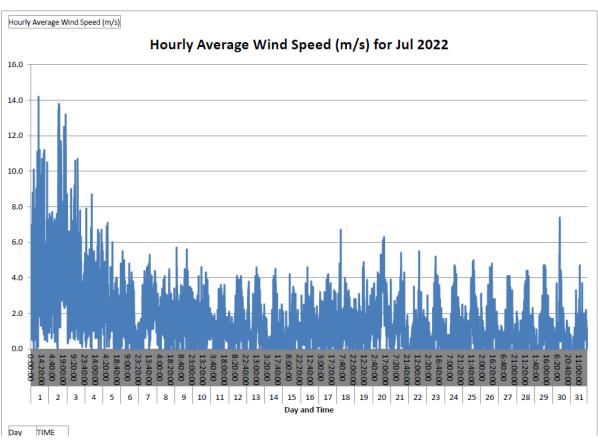

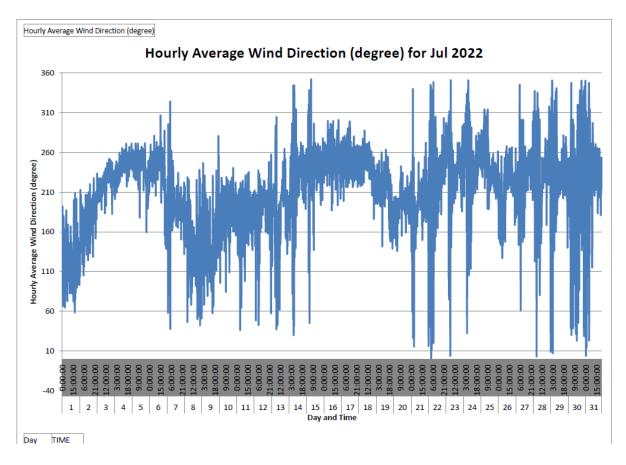

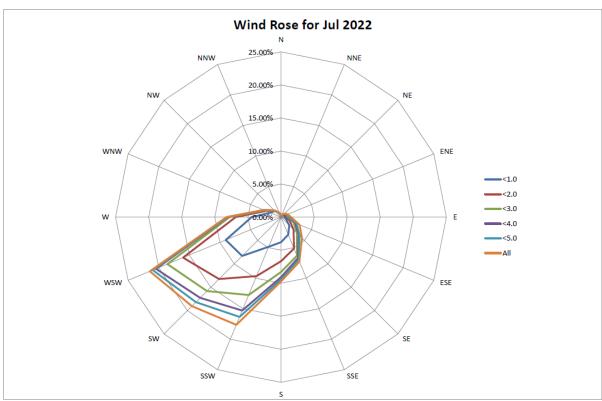

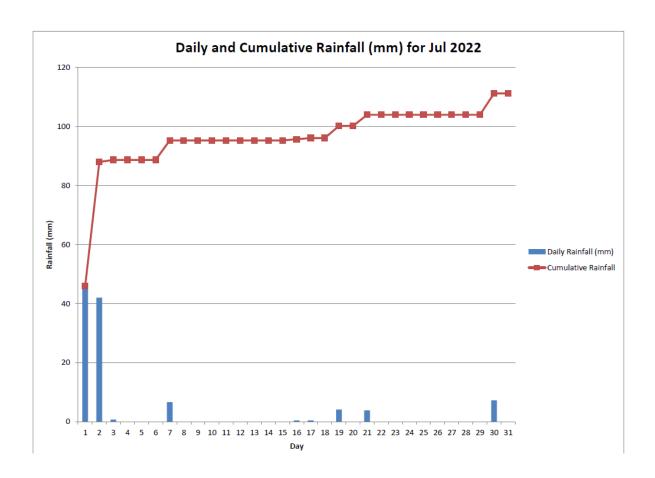

Annex D5

Certificates of the Qualified Odour Panelist



Certificate for a Qualified Odour Panellist

This is to certify that

LAU MEI TUNG

has participated in Ten (10) sets of individual N-Butanol Screening Test during 25 October 2021 - 03 November 2021

with Individual Threshold: 41 ppb/v

and

<u>fulfill</u> the Requirement of the European Standard Method of Air Quality – Determination of Odour Concentration by Dynamic Olfactometry (EN13725:2003) –

The Requirement of the Odour Threshold of n-Butanol in Nitrogen Gas in the Range of 20 - 80 ppb/v with at least 10 sets of individual threshold estimates and standard deviation less than 2.3

03 November 2021

Issue Date

03 November 2022

Valid Until

ung Lim Chee. Richard

Certificate No.: C21084

ALS Life Sciences | Environmental

Certificate No.: C21085

Certificate for a Qualified Odour Panellist

This is to certify that

WONG KA HEI

has participated in Ten (10) sets of individual N-Butanol Screening Test during 25 October 2021 - 03 November 2021

with Individual Threshold: 40 ppb/v

and

<u>fulfill</u> the Requirement of the European Standard Method of Air Quality – Determination of Odour Concentration by Dynamic Olfactometry (EN13725:2003) –

The Requirement of the Odour Threshold of n-Butanol in Nitrogen Gas in the Range of 20 - 80 ppb/v with at least 10 sets of individual threshold estimates and standard deviation less than 2.3

03 November 2021

Issue Date

03 November 2022

Valid Until

Fung Lim Chee, Richard



Certificate for a Qualified Odour Panellist

This is to certify that

WONG HO YU

has participated in Ten (10) sets of individual N-Butanol Screening Test during 25 October 2021 - 03 November 2021

with Individual Threshold: 56 ppb/v

and

<u>fulfill</u> the Requirement of the European Standard Method of Air Quality – Determination of Odour Concentration by Dynamic Olfactometry (EN13725:2003) –

The Requirement of the Odour Threshold of n-Butanol in Nitrogen Gas in the Range of 20 - 80 ppb/v with at least 10 sets of individual threshold estimates and standard deviation less than 2.3

03 November 2021

Issue Date

03 November 2022

Valid Until

ung Lim Chee, Richard

Certificate No.: C21086



Certificate for a Qualified Odour Panellist

This is to certify that

LAO KA LEONG

has participated in Ten (10) sets of individual N-Butanol Screening Test during 14 December 2021 - 20 December 2021

with Individual Threshold: 31 ppb/v

and

fulfill the Requirement of the European Standard Method of Air Quality -Determination of Odour Concentration by Dynamic Olfactometry (EN13725:2003) -

The Requirement of the Odour Threshold of n-Butanol in Nitrogen Gas in the Range of 20 - 80 ppb/v with at least 10 sets of individual threshold estimates and standard deviation less than 2.3

20 December 2021

Issue Date

20 December 2022

Valid Until

Certificate No.: C21094

Annex D6

Odour Monitoring Results

Table D6.1 Odour Monitoring Results

Date	Weather	Location	Time	Temperature	Wind Speed	Wind	From	Odour	Odour	Possible Source	Remarks
				(oC)	(m/s)	Direction	Project Site	Intensity	Characteristic		
22-Jul-22	Sunny	OP1	14:13	33.5	5.1	S	No	0	N/A	N/A	N/A
22-Jul-22	Sunny	OP2	14:16	33.5	5.1	S	No	0	N/A	N/A	N/A
22-Jul-22	Sunny	OP3	14:18	35.6	3.5	SW	No	0	N/A	N/A	N/A
22-Jul-22	Sunny	OP4	14:21	36.4	0.0	NA	NA	0	N/A	N/A	N/A
22-Jul-22	Sunny	OP5	14:24	36.8	1.1	W	No	0	N/A	N/A	N/A
22-Jul-22	Sunny	OP6	14:27	35.1	5.0	S	No	0	N/A	N/A	N/A
22-Jul-22	Sunny	OP7	14:30	34.3	5.4	S	No	0	N/A	N/A	N/A
22-Jul-22	Sunny	OP8	14:33	34.9	4.7	S	No	0	N/A	N/A	N/A
22-Jul-22	Sunny	OP9	14:36	35.4	4.0	SE	Yes	0	N/A	N/A	N/A
22-Jul-22	Sunny	OP10	14:39	38.0	2.3	E	Yes	1	Town gas	Town gas plant	N/A
22-Jul-22	Sunny	OP11	14:48	36.1	1.8	S	Yes	0	N/A	N/A	N/A

Annex D7

Thermal Oxidizer, Landfill Gas Flare and Landfill Gas Generator Stack Emission Monitoring Results

Table D7.1 Thermal Oxidiser Stack Emission Monitoring Results

Parameters	Monitoring Results	
NO ₂	0.89 gs ⁻¹	
CO	<0.01 gs ⁻¹	
SO ₂	<0.01 gs ⁻¹	
Benzene	$<2.1 \times 10^{-4} \text{ gs}^{-1}$	
Vinyl chloride	$< 2 \times 10^{-5} \text{ gs}^{-1}$	
Exhaust gas velocity	9.7 ms ⁻¹	

Table D7.2 Thermal Oxidiser Stack Continuous Monitoring Results

Date		Gas Combustion	Exhaust Temperature	Exhaust Gas
		Temperature (°C)	(K)	Velocity (ms-1) (a)
1 Jul 22		928	1168	
2 Jul 22		924	1167	
3 Jul 22		923	1165	
4 Jul 22		924	1171	
5 Jul 22		923	1172	
6 Jul 22		928	1171	
7 Jul 22		923	1170	
8 Jul 22		929	1171	
9 Jul 22		920	1169	
10 Jul 22		924	1172	
11 Jul 22		930	1172	
12 Jul 22		Under Maintenance		
13 Jul 22		Under Maintenance		
14 Jul 22		934	1169	
15 Jul 22		926	1170	
16 Jul 22		920	1168	9.7
17 Jul 22		928	1171	
18 Jul 22		929	1162	
19 Jul 22		918	1167	
20 Jul 22		932	1175	
21 Jul 22		924	1172	
22 Jul 22		918	1169	
23 Jul 22		924	1173	
24 Jul 22		927	1173	
25 Jul 22		925	1170	
26 Jul 22		924	1168	
27 Jul 22		925	1170	
28 Jul 22		930	1172	
29 Jul 22		922	1168	
30 Jul 22		924	1168	
31 Jul 22		927	1167	
	Average	925	1169	-
	Min	918	1162	-
	Max	934	1175	-

Notes:

(a) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring.

Table D7.3 Landfill Gas Flare Stack Emission Monitoring Results

Parameters	Monitoring Results (Flare 2 - F602)
NO ₂	<0.01 gs ⁻¹
CO	$0.53~{ m gs^{-1}}$
SO_2	0.01 gs ⁻¹
Benzene	<1.8 x 10 ⁻⁵ gs ⁻¹
Vinyl chloride	<1.4 x 10 ⁻⁵ gs ⁻¹
Exhaust gas velocity	6.5 ms ⁻¹

Table D7.4 Landfill Gas Flare Stack Continuous Monitoring Results

Date	Gas Combustion	Exhaust	Exhaust Gas	Operation Status
	Temperature (°C)	Temperature (K)	Velocity (ms-1) (a)	
Flare 1 - F6	501			
1 Jul 22	923	1029		In Operation
2 Jul 22	911	999		In Operation
3 Jul 22	891	1068		In Operation
4 Jul 22	899	1073		In Operation
5 Jul 22	902	1072		In Operation
6 Jul 22	822	1070		In Operation
7 Jul 22	947	1045		In Operation
8 Jul 22	894	990		In Operation
9 Jul 22	915	1037		In Operation
10 Jul 22	901	1057		In Operation
11 Jul 22	895	1025		In Operation
12 Jul 22	940	1063		In Operation
13 Jul 22	836	1060		In Operation
14 Jul 22	950	1033		In Operation
15 Jul 22	880	973		In Operation
16 Jul 22	900	1013	6.5	In Operation
17 Jul 22	885	1028		In Operation
18 Jul 22	920	1033		In Operation
19 Jul 22	950	1083		In Operation
20 Jul 22	920	1073		In Operation
21 Jul 22	890	1033		In Operation
22 Jul 22	880	1053		In Operation
23 Jul 22	920	1053		In Operation
24 Jul 22	900	1053		In Operation
25 Jul 22	890	1003		In Operation
26 Jul 22	955	998		In Operation
27 Jul 22	860	1033		In Operation
28 Jul 22	880	1013		In Operation
29 Jul 22	900	963		In Operation
30 Jul 22	860	993		In Operation
31 Jul 22	920	1063		In Operation
Average	901	1035	-	•
Min	822	963	-	
Max	955	1083	-	
Flare 2 - F6	502			
1 Jul 22	830	1073		In Operation
2 Jul 22	860	1073		In Operation
3 Jul 22	890	1113		In Operation
4 Jul 22	930	1153	6.5	In Operation
5 Jul 22	860	1103		In Operation
6 Jul 22	884	1109		In Operation
7 Jul 22	834	1068		In Operation

Date	Gas Combustion	Exhaust	Exhaust Gas	Operation Status
	Temperature (°C)	Temperature (K)	Velocity (ms-1) (a)	
8 Jul 22	830	1083		In Operation
9 Jul 22	870	1093		In Operation
10 Jul 22	830	1063		In Operation
11 Jul 22	905	1163		In Operation
12 Jul 22	840	1093		In Operation
13 Jul 22	870	1113		In Operation
14 Jul 22	840	1083		In Operation
15 Jul 22	824	1067		In Operation
16 Jul 22	834	1093		In Operation
17 Jul 22	904	1143		In Operation
18 Jul 22	865	1096		In Operation
19 Jul 22	845	1083		In Operation
20 Jul 22	880	1118		In Operation
21 Jul 22	854	1089		In Operation
22 Jul 22	830	1078		In Operation
23 Jul 22	880	1083		In Operation
24 Jul 22	830	1063		In Operation
25 Jul 22	842	1077		In Operation
26 Jul 22	844	1097		In Operation
27 Jul 22	854	1061		In Operation
28 Jul 22	875	1063		In Operation
29 Jul 22	835	1091		In Operation
30 Jul 22	874	1101		In Operation
31 Jul 22	860	1093		In Operation
Average	858	1093	-	
Min	824	1061	-	
Max	930	1163	-	

Notes:

⁽a) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring.

Table D7.5 Landfill Gas Generator Stack Emission Monitoring Results

Parameters	Monitoring Results	
NO ₂	0.01 gs ⁻¹	
CO	0.28 gs ⁻¹	
SO ₂	0.003 gs ⁻¹	
Benzene	<8.0 x 10 ⁻⁶ gs ⁻¹	
Vinyl chloride	<1.8 x 10 ⁻⁶ gs ⁻¹	
Exhaust gas velocity	11.2 ms ⁻¹	

Table D7.6 Landfill Gas Generator Stack Continuous Monitoring Results

Date	Exhaust	Exhaust Gas	Operation Status (Landfill
	Temperature (K)	Velocity (ms-1) (a)	Gas Generator in Operation)
1 Jul 22	867		In Operation (ENGA)
2 Jul 22	865		In Operation (ENGA)
3 Jul 22	869		In Operation (ENGA)
4 Jul 22	848		In Operation (ENGA)
5 Jul 22	852		In Operation (ENGA)
6 Jul 22	851		In Operation (ENGA)
7 Jul 22	884		In Operation (ENGA)
8 Jul 22	886		In Operation (ENGA)
9 Jul 22	887		In Operation (ENGA)
10 Jul 22	888		In Operation (ENGA)
11 Jul 22	889		In Operation (ENGA)
12 Jul 22	880		In Operation (ENGA)
13 Jul 22	880		In Operation (ENGA)
14 Jul 22	893		In Operation (ENGA)
15 Jul 22	871		In Operation (ENGB)
16 Jul 22	885	11.2	In Operation (ENGA)
17 Jul 22	886		In Operation (ENGA)
18 Jul 22	859		In Operation (ENGA)
19 Jul 22	866		In Operation (ENGA)
20 Jul 22	857		In Operation (ENGA)
21 Jul 22	857		In Operation (ENGA)
22 Jul 22	859		In Operation (ENGA)
23 Jul 22	860		In Operation (ENGA)
24 Jul 22	861		In Operation (ENGA)
25 Jul 22	863		In Operation (ENGA)
26 Jul 22	866		In Operation (ENGA)
27 Jul 22	859		In Operation (ENGA)
28 Jul 22	861		In Operation (ENGA)
29 Jul 22	859		In Operation (ENGA)
30 Jul 22	857		In Operation (ENGA)
31 Jul 22	860		In Operation (ENGA)
	nge 869	-	
	lin 848	-	
N	fax 893	-	

Notes:

(a) The exhaust gas velocity was calculated based on the cross-section area of the stack and the gas flow and combustion temperature data measured during the stack emission monitoring.

Annex D8

Investigation Reports of Environmental Quality Limit Exceedance

Investigation Report of Environmental Quality Limit Exceedance

Project	South East New Territories (SENT) Landfill Extension				
Date	29 July 2022				
Time	9:00 (29 July 2022) – 9:00 (30 July 2022)				
Monitoring Location	AM2, AM4				
Parameter	24-hour Total Suspended Particulates (TSP)				
Action / Limit Levels	Action level: >260 µg/ m ³				
·	Limit level: $>260 \mu g/m^3$				
Measured Level	AM2: 312 μg /m ³				
	AM4: $364 \mu g / m^3$				
Possible reason	From the meteorological data obtained from the SENTX on-site meteorological monitoring station, a predominantly southwesterly to west-southwesterly wind with highest wind speed 7.5 m/s was recorded on 29 and 30 July 2022 during the sampling event.				
	AM2 On 29 July 2022, the ET site representative observed that dust emitted from Cell 4X and the unpaved areas in the vicinity was blown toward dust monitoring station AM2. This could be the potential cause for the exceedance. Based on this observation, the TSP exceedance at AM2 was deemed to Project-related activities.				
	In accordance with Table 3.8b of the updated EM&A Manual, repeat measurement was conducted at AM2 on 4 August 2022 to confirm findings. The 24-hour TSP level was 36 µg/m³, which is well below Action/Limit Level. There is no consecutive exceedance at this dust monitoring location.				
	AM4 On 29 July 2022, the ET site representative observed that dust emitted from the public fill stockpiling areas and active earthworks from another project site in close vicinity of dust monitoring station AM4. No works from SENTX which may generate dust emission were conducted in the vicinity of AM4 on the sampling day based on the ET site representative on-site observations and the Contractor's record of the construction and operation activities carried out on that day.				
	Due to presence of the influencing factor from another project site and no Project-related dust emission source was identified in the vicinity of AM4, there is no adequate evidence showing that the exceedance at AM4 was due to Project-related activities.				
	In accordance with Table 3.8b of the updated EM&A Manual, repeat measurement was conducted at AM4 on 4 August 2022 to confirm findings. The 24-hour TSP level was 35 µg/m³, which is				

	well below the Action/Limit Level. There is no consecutive
	exceedance at this dust monitoring location.
Action Taken / Action to be Taken	In accordance with Table 3.8b of the updated EM&A Manual, the monitoring frequency at AM2 shall be increased to daily, until no exceedance of the Action/Limit Level. It should be noted that the turnaround time for the laboratory analysis of the dust filter paper is 5 working days and the preliminary results for the monitoring event conducted on 29 to 30 July 2022 were available on 4 August 2022. Repeat measurement was conducted on 4 August 2022 and the TSP monitoring result at AM2 is well below the Action/Limit Level. Hence, the daily TSP monitoring at AM2 shall not be triggered.
	Examination of environmental performance of the Project will be continued during the weekly inspections. The Contractor is reminded to implement relevant and appropriate mitigation measures according to the updated EM&A Manual to avoid any exceedance of the Action/Limit Level. In addition, the Contractor was reminded to discuss the dust control measures with CEDD to minimize the dust impact from the
	control measures with CEDD to minimize the dust impact from the other project site to proximity to the SENTX boundary.
Remarks	-

Prepared by: Abbey Lau
Designation: Environmental Team
Date: 17 August 2022

Annex E

Noise

Annex E1

Calibration Certificates for Noise Monitoring Equipment



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

校正證書

Certificate No.:

C215418

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC21-1345)

Date of Receipt / 收件日期: 26 August 2021

Description / 儀器名稱

Sound Calibrator (EQ083)

Manufacturer / 製造商 Model No. / 型號 Rion NC-74

Serial No. / 編號

34246492

Supplied By / 委託者

Action-United Environmental Services and Consulting

Unit A, 20/F., Gold King Industrial Building, 35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 温度 : (23 ± 2)°C

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$

Line Voltage / 電壓 : --

TEST SPECIFICATIONS / 測試規範

Calibration check

10 September 2021

TEST RESULTS / 測試結果

DATE OF TEST / 測試日期

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By

測試

K P Cheuk Project Engineer

Certified By 核證

K C Lee Engineer Date of Issue

13 September 2021

簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C215418

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID

CL130

CL281 TST150A Description

Universal Counter

Multifunction Acoustic Calibrator

C213954 AV210017

Measuring Amplifier

C201309

Certificate No.

Test procedure: MA100N. 4.

5. Results:

5.1 Sound Level Accuracy

Souther Editate Control			
UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	94.0	± 0.3	± 0.2

Frequency Accuracy 5.2

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	1.002	1 kHz ± 1 %	± 1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note:

Tel/電話: (852) 2927 2606

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

Fax/傳真: (852) 2744 8986

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C214361

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC21-1345)

Date of Receipt / 收件日期: 8 July 2021

Description / 儀器名稱

Sound Calibrator (EQ082)

Manufacturer / 製造商

Brüel & Kjær

Model No. / 型號

4231

Serial No. / 編號

2713428

Supplied By / 委託者

Action-United Environmental Services and Consulting

Unit A, 20/F., Gold King Industrial Building, 35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 :

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$

Line Voltage / 電壓

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST/測試日期

24 July 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By 測試

K P Cheuk

Project Engineer

Certified By 核證

C Lee

Date of Issue 簽發日期

26 July 2021

Engineer

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing, Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所 c/o 香港新界屯門興安里一號四樓



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C214361

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement 1. of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID

CL130

CL281 TST150A Description

Universal Counter

Multifunction Acoustic Calibrator

Certificate No. C213954

AV210017

Measuring Amplifier

C201309

4. Test procedure: MA100N.

5. Results:

Sound Level Accuracy 5.1

UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.1		

Frequency Accuracy

requestey recuracy			
UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	1 000 0	$1 \text{ kHz} \pm 0.1 \%$	± 0.1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing, Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所 c/o 香港新界屯門興安里一號四樓 Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C221365

證書編號

Date of Receipt / 收件日期: 14 February 2022

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC22-0258)

Description / 儀器名稱

Sound Level Meter (EQ018)

Manufacturer / 製造商

Rion

Model No. / 型號 Serial No./編號

NL-52 00809405

Supplied By / 委託者

Action-United Environmental Services and Consulting

Unit A, 20/F., Gold King Industrial Building, 35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(50 \pm 25)\%$

Line Voltage / 電壓

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

12 March 2022

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Fluke Everett Service Center, USA
- Agilent Technologies / Keysight Technologies

Tested By

測試

K C Lee Engineer

Certified By

核證

H C Chan

Date of Issue 簽發日期

Website/網址: www.suncreation.com

16 March 2022

Engineer

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C221365

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.

2. Self-calibration was performed before the test.

3. The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment:

Equipment ID

Description

Certificate No.

CL280

40 MHz Arbitrary Waveform Generator

C220381

CL281

Multifunction Acoustic Calibrator

AV210017

5. Test procedure: MA101N.

6. Results:

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

		Applied Value		UUT	IEC 61672		
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L_A	A	Fast	94.00	1	94.0	± 1.1

6.1.2 Linearity

	UU	Γ Setting		Applie	d Value	UUT
Range	Function	Frequency	Time	Level	Freq.	Reading
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)
30 - 130	L_{A}	A	Fast	94.00	1	94.0 (Ref.)
				104.00		104.0
-				114.00		114.0

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

	UUT Setting				Applied Value		IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L _A	A	Fast	94.00	1	94.0	Ref.
			Slow			94.0	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C221365

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

71- Weighting		Setting		Appl	ied Value	UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	_	(dB)	(dB)
30 - 130	L_A	A	Fast	94.00	63 Hz	67.8	-26.2 ± 1.5
					125 Hz	77.9	-16.1 ± 1.5
					250 Hz	85.4	-8.6 ± 1.4
		er.			500 Hz	90.8	-3.2 ± 1.4
	5				1 kHz	94.0	Ref.
					2 kHz	95.0	$+1.2 \pm 1.6$
					4 kHz	94.7	$+1.0 \pm 1.6$
-	-				8 kHz	92.9	-1.1 (+2.1; -3.1)
		90			16 kHz	85.5	-6.6 (+3.5 ; -17.0)

6.3.2 C-Weighting

UUT Setting			Applied Value		UUT	IEC 61672	
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
30 - 130	L_{C}	С	Fast	94.00	63 Hz	93.2	-0.8 ± 1.5
					125 Hz	93.9	-0.2 ± 1.5
		, I			250 Hz	94.0	0.0 ± 1.4
					500 Hz	94.1	0.0 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	93.6	-0.2 ± 1.6
			-		4 kHz	92.9	-0.8 ± 1.6
					8 kHz	91.0	-3.0 (+2.1; -3.1)
					16 kHz	83.5	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C221365

證書編號

Remarks: - UUT Microphone Model No.: UC-59 & S/N: 16463

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz : \pm 0.35 dB

104 dB : 1 kHz : \pm 0.10 dB (Ref. 94 dB) 114 dB : 1 kHz : \pm 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.


Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C215420

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC21-1765)

Date of Receipt / 收件日期: 26 August 2021

Description / 儀器名稱

Sound Level Meter (EQ013)

Manufacturer / 製造商

Rion

Model No./型號 Serial No. / 編號

NL-52 00921191

Supplied By / 委託者

Action-United Environmental Services and Consulting

Unit A, 20/F., Gold King Industrial Building, 35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

10 September 2021

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By 測試

K P Cheuk

Project Engineer

Certified By 核證

K C Lee Engineer Date of Issue

13 September 2021

簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

Certificate No.: C215420

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to 1. warm up for over 10 minutes before the commencement of the test.

2. Self-calibration was performed before the test.

3. The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment:

Equipment ID

Description

Certificate No.

CL280

40 MHz Arbitrary Waveform Generator

C210084

CL281

Multifunction Acoustic Calibrator

AV210017

5. Test procedure: MA101N.

6. Results:

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

	UUT Setting				Applied Value		IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	LA	A	Fast	94.00	1	94.2	± 1.1

6.1.2 Linearity

	UU'	T Setting	Applied	d Value	UUT	
Range	Function	Frequency	Time	Level	Freq.	Reading
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)
30 - 130	L_A	A	Fast	94.00	1	94.2 (Ref.)
	* Sweet			104.00		104.2
				114.00		114.1

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

	UUT Setting			Applied Value		UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L _A	A	Fast	94.00	1	94.2	Ref.
			Slow			94.2	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C215420

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

	UUT Setting			Applied Value		UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
30 - 130	L_A	A	Fast	94.00	63 Hz	67.9	-26.2 ± 1.5
					125 Hz	78.0	-16.1 ± 1.5
					250 Hz	85.5	-8.6 ± 1.4
					500 Hz	91.0	-3.2 ± 1.4
					1 kHz	94.2	Ref.
					2 kHz	95.4	$+1.2 \pm 1.6$
					4 kHz	95.2	$+1.0 \pm 1.6$
					8 kHz	93.2	-1.1 (+2.1; -3.1)
					16 kHz	86.2	-6.6 (+3.5 ; -17.0)

6.3.2 C-Weighting

C Westing.	UUT Setting				Applied Value		IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)		(dB)	(dB)
30 - 130	L_{C}	С	Fast	94.00	63 Hz	93.3	-0.8 ± 1.5
					125 Hz	94.0	-0.2 ± 1.5
					250 Hz	94.2	0.0 ± 1.4
					500 Hz	94.2	0.0 ± 1.4
					1 kHz	94.2	Ref.
					2 kHz	94.0	-0.2 ± 1.6
					4 kHz	93.4	-0.8 ± 1.6
					8 kHz	91.3	-3.0 (+2.1; -3.1)
					16 kHz	84.3	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C215420

證書編號

Remarks: - UUT Microphone Model No.: UC-59 & S/N: 12910

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz : \pm 0.35 dB

 $\begin{array}{lll} 250 \ Hz - 500 \ Hz & : \pm 0.30 \ dB \\ 1 \ kHz & : \pm 0.20 \ dB \\ 2 \ kHz - 4 \ kHz & : \pm 0.35 \ dB \\ 8 \ kHz & : \pm 0.45 \ dB \\ 16 \ kHz & : \pm 0.70 \ dB \end{array}$

104 dB : 1 kHz : $\pm 0.10 \text{ dB}$ (Ref. 94 dB) 114 dB : 1 kHz : $\pm 0.10 \text{ dB}$ (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Annex E2


Noise Monitoring Results

Table E2.1 Measured Noise Levels (dB(A)) at NM1 during Normal Working Hours (0700-1900 hours; Normal Weekdays)

Date	Start Time	Finish Time	Weather	$L_{10~(30min)}$	$L_{90~(30min)}$	Leq (30min)
6 Jul 22	14:02	14:32	Cloudy	55.8	52.7	54.4
12 Jul 22	14:36	15:06	Sunny	53.2	48.1	51.5
18 Jul 22	9:48	10:18	Sunny	54.5	51.2	53.3
25 Jul 22	10:32	11:02	Sunny	53.9	49.9	52.2
					Average 52.9	
					Miı	n 51.5
					Max	x 54.4

Correction of +3 dB(A) was made for free field measurements.

Graphical Presentation for Noise Monitoring at NM1 Figure E2.1

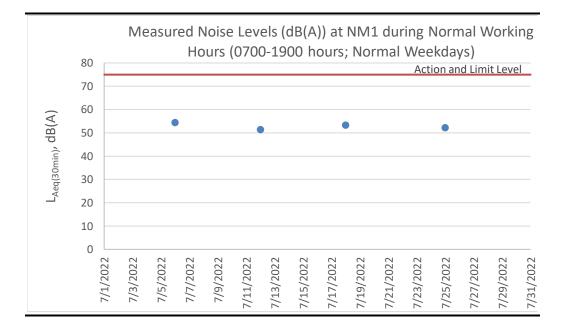

Annex E3

Event and Action Plan for Noise Monitoring

Annex E3 Event and Action Plan for Operational Noise Monitoring

Event	Action								
	ET	IEC	Contractor						
Action Level	 Identify the source(s) and investigate the cause(s) of exceedance and complaint Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Have additional monitoring if exceedance is due to the Project. If exceedance stops, cease additional monitoring 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Submit proposals for remedial measures to IEC Implement the agreed proposals 						
Limit Level	 Identify the source(s) and investigate the cause(s) of exceedance and complaint Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD whether the cause of exceedance is due to the Project Analyse the operation of SENTX and investigate the causes of exceedance Provide interim report to Contractor, IEC, Project Proponent and EPD the causes of the exceedances Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Report the remedial measures implemented and the additional monitoring results to Contactor, IEC, Project Proponent and EPD Have additional monitoring if exceedance is due to the Project. If exceedance stops, cease additional monitoring 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Take immediate measures to avoid further exceedance Submit proposals for remedial measures to IEC within 3 working days of notification Implement the agreed proposals Resubmit proposals if problem still not under control Stop the relevant activity of works as determined by the Project Proponent until the exceedance is abated 						

Surface Water Quality

Calibration Certificates for Surface Water Quality Monitoring Equipment



ALS Technichem (HK) Pty Ltd

11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street, Kwai Chung N.T., Hong Kong

T: +852 2610 1044 | F: +852 2610 2021

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR BEN TAM WORK ORDER: HK2214108

CLIENT: ACTION-UNITED ENVIRONMENTAL SERVICES &

CONSULTING

ADDRESS: RM A 20/F., GOLD KING IND BLDG, SUB-BATCH: 0

NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. LABORATORY: HONG KONG

DATE RECEIVED: 21-Apr-2022 DATE OF ISSUE: 26-Apr-2022

SPECIFIC COMMENTS

Equipment information (Brand name, Model No., Serial No. and Equipment No.) is provided by client.

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the laboratory or quoted from relevant international standards.

The validity of equipment/ meter performance only applies to the result(s) stated in the report.

Equipment Type: Multifunctional Meter Service Nature: Performance Check

Scope: Conductivity, Dissolved Oxygen, pH Value, Turbidity, Salinity and Temperature

Brand Name/ Model No.: [YSI]/ [Professional DSS]

Serial No./ Equipment No.: [20]101862/15H103928]/ [EQW018]

Date of Calibration: 26-April-2022

GENERAL COMMENTS

This report superseded any previous report(s) with same work order number.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganics

 $This\ report\ may\ not\ be\ reproduced\ except\ with\ prior\ written\ approval\ from\ ALS\ Technichem\ (HK)\ Pty\ Ltd.$

WORK ORDER: HK2214108

SUB-BATCH: 0

DATE OF ISSUE: 26-Apr-2022

CLIENT: ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[YSI]/ [Professional DSS]

Serial No./ Equipment No.:

[20J101862/15H103928]/[EQW018]

Date of Calibration: 26-April-2022 Date of Next Calibration: 26-July-2022

PARAMETERS:

Conductivity Method Ref: APHA (21st edition), 2510B

Expected Reading (µS/cm)	Displayed Reading (µS/cm)	Tolerance (%)
146.9	153.1	+4.2
6667	6431	-3.5
12890	12657	-1.8
58670	56091	-4.4
	Tolerance Limit (%)	±10.0

Dissolved Oxygen

Method Ref: APHA (21st edition), 45000: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.30	3.47	+0.17
5.56	5.67	+0.11
8.18	8.20	+0.02
	Tolerance Limit (mg/L)	±0.20

pH Value Method Ref: APHA (21st edition), 4500H: B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)
4.0	3.83	-0.17
7.0	7.08	+0.08
10.0	9.97	-0.03
	Tolerance Limit (pH unit)	±0.20

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganics

WORK ORDER: HK2214108

SUB-BATCH: 0

DATE OF ISSUE: 26-Apr-2022

CLIENT: ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[YSI]/ [Professional DSS]

Serial No./ Equipment No.:

[20J101862/15H103928]/[EQW018]

Date of Calibration: 26-April-2022 Date of Next Calibration: 26-July-2022

PARAMETERS:

Turbidity Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.00	
4	4.13	+3.3
40	41.69	+4.2
80	76.20	-4.8
400	403.20	+0.8
800	764.91	-4.4
	Tolerance Limit (%)	±10.0

Salinity Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	
10	10.03	+0.3
20	20.38	+1.9
30	30.29	+1.0
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganics

WORK ORDER: HK2214108

SUB-BATCH: 0

DATE OF ISSUE: 26-Apr-2022

CLIENT: ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[YSI]/ [Professional DSS]

Serial No./ Equipment No.:

[20J101862/15H103928]/[EQW018]

Date of Calibration: 26-April-2022 Date of Next Calibration: 26-July-2022

PARAMETERS:

Temperature Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
7.5	8.2	+0.7
23.5	22.4	-1.1
38.0	36.5	-1.5
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

16:3

Ms. Lin Wai Yu, Iris Assistant Manager - Inorganics

Surface Water Quality Monitoring Results

Table F2.1 Surface Water Quality Monitoring Results at DP4

Date	Time	Weather	Water	Water	Water	Ammoniacal-	COD	Suspended	Remarks
		Condition	Appearance	Condition	Temperature	nitrogen (mg/L)		Solids (SS)	
					(oC)			(mg/L)	
8 Jul 22	10:45	Sunny	Light Yellow	Semi-clear	-	-	-	26.3	-
15 Jul 22	10:30	Sunny	Light Yellow	Semi-clear	-	-	-	7.1	-
25 Jul 22	09:30	Sunny		Unable to co	ollect water sam	ple due to insuffic	cient flow		-
					Average	-	-	16.7	-
					Min	-	-	7.1	-
					Max	-	-	26.3	-

Table F2.2 Surface Water Quality Monitoring Results at DP6

Date	Time	Weather Condition	Water Appearance	Water Condition	Water Temperature (oC)	Ammoniacal- nitrogen (mg/L)	COD	Suspended Solids (SS) (mg/L)	Remarks
25 Jul 22	09:39	Sunny		Unable to	collect water sam	ple due to insuffi	cient flow		-
					Average	? -	-	-	-
					Min	1 <i>-</i>	-	-	-
					Max	6 -	-	-	-

Event and Action Plan for Surface Water Quality Monitoring

Annex F3 Event and Action Plan for Water Quality Monitoring During Operation/Restoration Phase

Event	Action						
	ET	IEC	Contractor				
Exceedance of Limit Level for urface water nonitoring	 Identify source(s) of impact and investigate the cause(s) of exceedance Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Repeat measurement to confirm finding if exceedance is due to the Project Increase monitoring frequency to weekly if exceedance is due to the Project until no exceedance of Limit Level 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Check Contractor's working methods Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Take immediate action to avoid further exceedance Submit proposals for remedial measures to IEC Implement the agreed proposals Amend proposal if appropriate 				
Exceedance of Limit Level for groundwater nonitoring	 Identify source(s) of impact and investigate the cause(s) of exceedance Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Repeat measurement to confirm finding if exceedance is due to the Project Increase monitoring frequency to weekly if exceedance is due to the Project until no exceedance of Limit Level 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Check Contractor's working methods Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Divert groundwater collected at the collection sumps to the leachate treatment plant Submit proposals for remedial measures to IEC Rectify any unacceptable practice or design Amend working methods as required Implement amended working methods, if necessary 				

ENVIRONMENTAL RESOURCES MANAGEMENT

GREEN VALLEY LANDFILL LTD.

Event	Action						
	ET	IEC	Contractor				
Exceedance of Limit Level for leachate level	 Investigate the cause(s) of exceedance Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented 	 Verify the Notification of Exceedance Check with Contractor on the operating activities and performance of the leachate collection system Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Check the performance of the leachate collection system Rectify any unacceptable practice; Amend leachate collection design if required Implement amended leachate collection system, if necessary 				
Exceedance of Limit Level of effluent discharge from LTP	 Investigate the cause(s) of exceedance Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Repeat measurement to confirm finding if exceedance is due to the Project Increase monitoring frequency to weekly until no exceedance of Limit Level 	 Verify the Notification of Exceedance Check with Contractor on the operation performance of the LTP Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Rectify any unacceptable practice; Carry out remedial measures or amend design as required Implement amended design, if necessary 				

ENVIRONMENTAL RESOURCES MANAGEMENT

GREEN VALLEY LANDFILL LTD.

Calibration Certificates for Effluent Quality Monitoring Equipment



ALS Technichem (HK) Pty Ltd

11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street, Kwai Chung N.T., Hong Kong T: +852 2610 1044 | F: +852 2610 2021

,

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR IVAN LEUNG WORK ORDER: HK2212038

CLIENT: ALS TECHNICHEM (HK) PTY LTD

ADDRESS: 11/F., CHUNG SHUN KNITTING CENTRE, SUB-BATCH: 0

1-3 WING YIP STREET, KWAI CHUNG, N.T. LABORATORY: HONG KONG

DATE RECEIVED: 06-Apr-2022
DATE OF ISSUE: 14-Apr-2022

SPECIFIC COMMENTS

Equipment information (Brand name, Model No., Serial No. and Equipment No.) is provided by client.

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the laboratory or quoted from relevant international standards.

The validity of equipment/ meter performance only applies to the result(s) stated in the report.

Equipment Type: Multifunctional Meter Service Nature: Performance Check

Scope: Conductivity, Dissolved Oxygen, pH Value, Redox Potential and Temperature

Brand Name/ Model No.: [LUTRON]/ [WA-2017SD]
Serial No./ Equipment No.: [T.016811]/ [HK2009]

Date of Calibration: 14-April-2022

GENERAL COMMENTS

This report superseded any previous report(s) with same work order number.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganics

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

WORK ORDER: HK2212038

SUB-BATCH: C

DATE OF ISSUE: 14-Apr-2022

CLIENT: ALS TECHNICHEM (HK) PTY LTD

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

Equipment No.:

[LUTRON]/ [WA-2017SD]

Serial No./

[T.016811]/ [HK2009]

Date of Calibration: 14-April-2022 Date of Next Calibration: 14-July-2022

PARAMETERS:

Conductivity Method Ref: APHA (21st edition), 2510B

Expected Reading (µS/cm)	Displayed Reading (µS/cm)	Tolerance (%)
146.9	144.1	-1.9
6667	6560	-1.6
12890	12270	-4.8
58670	55800	-4.9
	Tolerance Limit (%)	±10.0

Dissolved Oxygen

Method Ref: APHA (21st edition), 45000: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)		
3.29	3.1	-0.19		
5.80	5.6	-0.20		
8.30	8.2	-0.10		
	Tolerance Limit (mg/L)	±0.20		

pH Value Method Ref: APHA (21st edition), 4500H: B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)		
4.0	4.04	+0.04		
7.0	7.08	+0.08		
10.0	9.99	-0.01		
	Tolerance Limit (pH unit)	±0.20		

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganic

WORK ORDER: HK2212038

SUB-BATCH: 0

DATE OF ISSUE: 14-Apr-2022

CLIENT: ALS TECHNICHEM (HK) PTY LTD

Equipment Type:

Multifunctional Meter

Brand Name/ Model No.:

[LUTRON]/ [WA-2017SD]

Serial No./ Equipment No.:

[T.016811]/ [HK2009]

Date of Calibration:

2, 2

14-April-2022

PARAMETERS:

Redox Potential

Method Ref: APHA (21st edition), 2580B

Method Ref: Orion Research Instruction Manual and the Laboratory Manual

the Environmental of Water, Wastewater and Soil (2nd edition), Rump & Krist (1992)

_	•	, , ,	1 ,
	Expected Reading (mV)	Displayed Reading (mV)	Difference of A and B (mV)
	Solution A (~234mV)	230	
	Solution B (~300mV)	301	+71.0
		Tolerance Limit (mV)	>66

Date of Next Calibration:

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)		
7.0	7.4	+0.4		
22.0	22.2	+0.2		
39.0	38.9	-0.1		
	Tolerance Limit (°C)	±2.0		

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

/ /: 5

14-July-2022

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganic



ALS Technichem (HK) Pty Ltd

11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street, Kwai Chung N.T., Hong Kong T: +852 2610 1044 | F: +852 2610 2021

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR IVAN LEUNG WORK ORDER: HK2225127

CLIENT: ALS TECHNICHEM (HK) PTY LTD

ADDRESS: 11/F., CHUNG SHUN KNITTING CENTRE, SUB-BATCH: 0

1-3 WING YIP STREET, KWAI CHUNG, N.T. LABORATORY: HONG KONG

DATE RECEIVED: 04-Jul-2022
DATE OF ISSUE: 06-Jul-2022

SPECIFIC COMMENTS

Equipment information (Brand name, Model No., Serial No. and Equipment No.) is provided by client.

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the laboratory or quoted from relevant international standards.

The validity of equipment/ meter performance only applies to the result(s) stated in the report.

Equipment Type: pH meter

Service Nature: Performance Check

Scope: pH Value and Temperature

Brand Name/ Model No.: [TOA]/ [HM-30P]
Serial No./ Equipment No.: [790332]/ [HK1383]

Date of Calibration: 05-July-2022

GENERAL COMMENTS

This report superseded any previous report(s) with same work order number.

Mr Chan Siu Ming, Vico Manager - Inorganics

Na Ship

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

WORK ORDER: HK2225127

SUB-BATCH: 0

DATE OF ISSUE: 06-Jul-2022

CLIENT: ALS TECHNICHEM (HK) PTY LTD

Equipment Type: pH meter

Brand Name/ Model No.:

[TOA]/ [HM-30P]

Serial No./ Equipment No.:

[790332]/[HK1383]

Date of Calibration: 05-July-2022 Date of Next Calibration: 05-October-2022

PARAMETERS:

pH Value Method Ref: APHA (21st edition), 4500H: B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)		
4.0	4.03	+0.03		
7.0	6.89	-0.11		
10.0	10.04	+0.04		
	Tolerance Limit (pH unit)	±0.20		

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)		
7.5	7.5	+0.0		
22.5	21.8	-0.7		
38.0	37.8	-0.2		
	Tolerance Limit (°C)	±2.0		

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr Chan Siu Ming, Vico Manager - Inorganics

Ma Si

Leachate Levels Monitoring Results

Table F5.1 Leachate Levels Monitoring Results (Pump Station No.1X (Cell 1X))

Date	Meter No.X1 (cm)	Meter No.X2 (cm)	Average (cm)
Pump Station No. 1X	(Cell 1X)		
1-Jul-22	55	75	65
2-Jul-22	55	75	65
3-Jul-22	55	75	65
4-Jul-22	55	75	65
5-Jul-22	68	88	78
6-Jul-22	57	77	67
7-Jul-22	62	82	72
8-Jul-22	68	88	78
9-Jul-22	59	77	68
10-Jul-22	46	66	56
11-Jul-22	46	66	56
12-Jul-22	53	75	64
13-Jul-22	57	79	68
14-Jul-22	59	79	69
15-Jul-22	59	79	69
16-Jul-22	57	77	67
17-Jul-22	48	68	58
18-Jul-22	48	68	58
19-Jul-22	68	88	78
20-Jul-22	68	88	78
21-Jul-22	46	66	56
22-Jul-22	46	66	56
23-Jul-22	55	75	65
24-Jul-22	48	68	58
25-Jul-22	48	68	58
26-Jul-22	73	86	80
27-Jul-22	66	79	73
28-Jul-22	57	70	64
29-Jul-22	73	86	80
30-Jul-22	64	77	71
31-Jul-22	64	73	69
Average		76	67
Mir	1 46	66	56
Max	c 73	88	80

Table F5.2 Leachate Levels Monitoring Results (Pump Station No.2X (Cell 2X))

Date	Meter No.X3 (cm)	Meter No.X4 (cm)	Average (cm)
Pump Station N	No. 2X (Cell 2X)		
1-Jul-22	64	66	65
2-Jul-22	64	66	65
3-Jul-22	64	66	65
4-Jul-22	64	66	65
5-Jul-22	62	66	64
6-Jul-22	82	88	85
7-Jul-22	82	88	85
8-Jul-22	73	77	75
9-Jul-22	64	70	67
10-Jul-22	79	85	82
11-Jul-22	79	85	82
12-Jul-22	79	84	82
13-Jul-22	75	79	77
14-Jul-22	68	73	71
15-Jul-22	59	64	62
T			C

ENVIRONMENTAL RESOURCES MANAGEMENT

GREEN VALLEY LANDFILL LTD.

Date		Meter No.X3 (cm)	Meter No.X4 (cm)	Average (cm)
16-Jul-22		79	86	83
17-Jul-22		84	90	87
18-Jul-22		84	90	87
19-Jul-22		73	77	75
20-Jul-22		86	90	88
21-Jul-22		73	79	76
22-Jul-22		86	90	88
23-Jul-22		70	77	74
24-Jul-22		66	73	70
25-Jul-22		66	73	70
26-Jul-22		77	84	81
27-Jul-22		57	64	61
28-Jul-22		70	77	74
29-Jul-22		79	86	83
30-Jul-22		59	64	62
31-Jul-22		86	90	88
	Average	73	78	75
	Min	57	64	61
	Max	86	90	88

Table F5.3 Leachate Levels Monitoring Results (Pump Station No.3X (Cell 3X))

Date		Meter No.X5 (cm)	Meter No.X6 (cm)	Average (cm)
Pump Stati	on No. 3X	(Cell 3X)		-
1-Jul-22		53	73	63
2-Jul-22		53	73	63
3-Jul-22		53	73	63
4-Jul-22		53	73	63
5-Jul-22		75	75	75
6-Jul-22		75	75	75
7-Jul-22		73	73	73
8-Jul-22		70	70	70
9-Jul-22		70	70	70
10-Jul-22		73	73	73
11-Jul-22		73	73	73
12-Jul-22		70	70	70
13-Jul-22		75	75	75
14-Jul-22		75	75	75
15-Jul-22		68	68	68
16-Jul-22		68	68	68
17-Jul-22		66	66	66
18-Jul-22		66	66	66
19-Jul-22		68	68	68
20-Jul-22		70	70	70
21-Jul-22		70	70	70
22-Jul-22		68	68	68
23-Jul-22		62	62	62
24-Jul-22		75	75	75
25-Jul-22		75	75	75
26-Jul-22		64	64	64
27-Jul-22		68	68	68
28-Jul-22		70	70	70
29-Jul-22		70	70	70
30-Jul-22		70	70	70
31-Jul-22		64	64	64
	Average	68	70	69
	Min	53	62	62
	Max	75	75	75

Effluent Quality Monitoring Results

Table F6.1 Effluent Monitoring Results

		1 Jul 22	3 Jul 22	4 Jul 22	5 Jul 22	6 Jul 22	7 Jul 22	8 Jul 22	9 Jul 22	11 Jul 22	12 Jul 22	13 Jul 22
On-site Measurement	s											
Temperature	°C	30.8	30.3	25.0	34.3	33.0	35.3	34.3	34.8	31.2	34.6	32.5
pH Value	pH Unit	8.4	8.3	8.4	8.4	8.4	8.4	8.4	8.4	8.6	8.4	8.2
Volume Discharged	m^3	1,227	1,552	1,051	905	1,059	1,073	926	793	364	41	46
Laboratory Analysis												
Suspended Solids (SS)	mg/L	17.9	61.8	15.6	20.8	21.4	27.1	20.3	38.9	7.6	17.0	15.2
Alkalinity	mg/L	1790	1260	1080	1300	1360	1470	1500	1600	1700	1720	1730
Ammoniacal-nitrogen	mg/L	1.05	0.31	0.42	0.45	0.37	0.16	0.26	0.29	0.29	0.33	0.53
Chloride	mg/L	1730	1450	1210	1490	1500	1580	1660	1740	1820	1620	1600
Nitrite-nitrogen	mg/L	1.23	0.08	0.16	0.08	0.10	0.08	0.09	0.15	0.28	0.34	0.32
Phosphate	mg/L	4.04	4.18	2.47	1.96	2.49	2.50	3.22	3.23	2.87	3.00	4.44
Sulphate	mg/L	290	281	340	470	459	458	390	339	315	276	282
Total Nitrogen	mg/L	101.0	110.0	103.0	88.0	90.7	93.0	105.0	91.1	95.1	105.0	108.0
Nitrate-nitrogen	mg/L	45.1	68.5	60.7	46.4	61.6	46.9	62.1	49.5	53.3	61.4	59.6
Total Inorganic												
Nitrogen	mg/L	47.38	68.89	61.28	46.93	62.07	47.14	62.45	49.94	53.87	62.07	60.45
Biochemical Oxygen												
Demand (BOD)	mg/L	5	10	9	7	6	9	5	7	8	8	11
Chemical Oxygen												
Demand (COD)	mg/L	861	739	608	671	639	702	709	674	758	779	739
Oil & Grease	mg/L	<5	<5	<5	<5	<5	<5	<5	<5	<5	<5	<5
Total Organic Carbon												
(TOC)	mg/L	344	280	252	186	284	290	286	317	309	254	260
Boron	μg/L	4820	3930	3500	3770	3880	3840	3860	4060	4440	4610	4580
Calcium	mg/L	39.6	46.0	64.0	60.8	57.6	53.9	49.6	47.1	43.4	43.0	43.1
Iron	mg/L	1.72	1.28	1.04	1.06	1.17	1.27	1.30	1.37	1.24	1.39	1.37
Magnesium	mg/L	25.0	25.8	24.6	25.3	26.3	26.9	26.8	26.3	25.1	26.2	26.2
Potassium	mg/L	782	624	524	589	634	639	665	682	714	737	737
Cadmium	μg/L	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0
Chromium	μg/L	103	79	67	75	80	86	88	91	93	90	89
Copper	μg/L	<10	<10	<10	<10	<10	<10	<10	21	<10	20	11
Nickel	μg/L	96	71	62	74	84	84	88	91	95	100	102
Zinc	μg/L	79	79	62	65	72	70	68	94	70	104	104

		14 Jul 22	15 Jul 22	16 Jul 22	17 Jul 22	18 Jul 22	19 Jul 22	20 Jul 22	21 Jul 22	22 Jul 22	23 Jul 22	24 Jul 22	25 Jul 22
On-site Measureme	ents	-											
Temperature	°C	33.8	33.7	35.0	35.0	34.0	32.0	36.5	36.9	30.8	30.4	30.4	38.1
pH Value	pH Unit	8.3	8.3	8.2	8.2	8.3	8.3	8.3	8.3	8.5	8.6	8.6	8.5
Volume Discharged	m³	108	1,197	1,176	1,126	830	789	1,077	1,303	1,309	1,312	1,316	1,192
Laboratory Analysi	s												
Suspended Solids	1												
(SS)	mg/L	7.8	26.0	26.8	95.2	18.3	24.1	24.4	18.8	25.8	14.5	61.0	19.5
Alkalinity	mg/L	1730	1700	1800	1820	1940	2000	2100	2050	2150	2120	2110	2230
Ammoniacal-													
nitrogen	mg/L	0.52	0.42	0.29	0.70	0.26	0.25	0.34	0.65	0.32	0.33	0.34	0.50
Chloride	mg/L	1640	1680	1800	1870	1870	1700	1760	1870	2000	2030	1950	2020
Nitrite-nitrogen	mg/L	0.47	0.12	0.12	0.13	0.14	0.11	0.11	0.12	0.14	0.16	0.12	0.16
Phosphate	mg/L	4.54	4.72	4.94	5.14	5.41	5.46	5.58	5.83	5.11	5.40	5.33	5.44
Sulphate	mg/L	303	283	258	274	220	162	172	202	186	198	176	182
Total Nitrogen	mg/L	97.2	90.6	92.2	99.4	98.0	92.1	95.0	97.4	109.0	106.0	111.0	111.0
Nitrate-nitrogen	mg/L	53.2	47.7	45.8	46.4	49.1	46.4	43.2	49.5	54.7	50.7	52.6	54.1
Total Inorganic													
Nitrogen	mg/L	54.19	48.24	46.21	47.23	49.50	46.76	43.65	50.27	55.16	51.19	53.06	54.76
Biochemical Oxyger													
Demand (BOD)	mg/L	11	11	12	8	6	9	8	3	6	4	13	7
Chemical Oxygen	0.												
Demand (COD)	mg/L	641	739	770	746	840	832	899	837	887	940	953	997
Oil & Grease	mg/L	<5	<5	<5	<5	<5	<5	<5	<5	<5	<5	<5	<5
Total Organic	_												
Carbon (TOC)	mg/L	304	309	320	359	354	348	380	374	366	380	394	401
Boron	μg/L	4620	4620	4680	4530	4920	4790	5040	5160	5570	5220	5970	6020
Calcium	mg/L	41.0	44.3	40.5	39.2	32.2	36.1	33.5	36.5	29.0	30.6	33.0	29.6
Iron	mg/L	1.24	1.46	1.39	1.60	1.40	1.57	1.55	1.52	1.56	1.67	1.74	1.79
Magnesium	mg/L	23.8	29.4	30.5	30.4	27.7	27.8	29.1	30.1	26.1	27.5	29.4	27.4
Potassium	mg/L	711	738	739	734	740	789	829	849	786	828	858	923
Cadmium	μg/L	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0
Chromium	μg/L	89	92	97	104	106	104	105	106	114	123	122	133
Copper	μg/L	<10	<10	11	<10	<10	<10	<10	<10	17	63	64	<10
Nickel	μg/L	98	96	104	103	108	104	105	107	114	120	119	127
Zinc	μg/L	70	72	82	88	73	76	69	74	81	105	108	78

		26 Jul 22	27 Jul 22	28 Jul 22	29 Jul 22	30 Jul 22	31 Jul 22
On-site Measuremen	nts	- y-		<u> </u>	,		
Temperature	°C	38.1	37.8	35.7	35.5	34.9	32.5
pH Value	pH Unit	8.2	8.2	8.4	8.4	8.5	8.5
Volume Discharged	m ³	1,192	1,010	1,074	1,273	1,086	1,127
Laboratory Analysis		•	•	,	•	•	,
Suspended Solids							
(SS)	mg/L	33.5	45.5	40.5	41.6	37.9	40.8
Alkalinity	mg/L	2220	2310	2320	2310	2270	2310
Ammoniacal-							
nitrogen	mg/L	0.54	0.49	0.35	0.59	0.49	0.55
Chloride	mg/L	1920	2070	2000	1990	2000	2000
Nitrite-nitrogen	mg/L	0.16	0.13	0.14	0.14	0.16	0.16
Phosphate	mg/L	5.7	5.41	5.74	6.4	6.53	5.72
Sulphate	mg/L	157	165	174	171	197	186
Total Nitrogen	mg/L	104.0	103	100.0	103.0	107.0	110.0
Nitrate-nitrogen	mg/L	55	56.8	47.5	48.1	49.2	48.9
Total Inorganic	O,						
Nitrogen	mg/L	55.70	57.42	47.99	48.83	49.85	49.61
Biochemical Oxygen	_						
Demand (BOD)	mg/L	9	10	10	8	7	8
Chemical Oxygen	_						
Demand (COD)	mg/L	990	1040	963	973	978	953
Oil & Grease	mg/L	<5	<5	<5	<5	<5	<5
Total Organic	_						
Carbon (TOC)	mg/L	382	434	424	395	394	412
Boron	μg/L	5570	5260	5100	5560	5550	5620
Calcium	mg/L	28.1	23.8	27.3	26.6	27.4	26.4
Iron	mg/L	1.93	1.7	1.77	1.85	1.82	1.83
Magnesium	mg/L	29.8	23.4	26.3	25.8	26.6	26.4
Potassium	mg/L	871	794	904	877	900	890
Cadmium	μg/L	<1.0	<1.0	<1.0	<1.0	<1.0	<1.0
Chromium	μg/L	129	124	115	122	126	127
Copper	μg/L	<10	15	<10	<10	<10	<10
Nickel	μg/L	126	114	109	113	116	118
Zinc	μg/L	84	84	64	68	66	69

Calibration Certificates for Groundwater Monitoring Equipment



ALS Technichem (HK) Pty Ltd

11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street, Kwai Chung N.T., Hong Kong

T: +852 2610 1044 | F: +852 2610 2021

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR BEN TAM WORK ORDER: HK2214108

CLIENT: ACTION-UNITED ENVIRONMENTAL SERVICES &

CONSULTING

ADDRESS: RM A 20/F., GOLD KING IND BLDG, SUB-BATCH: 0

NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. LABORATORY: HONG KONG

DATE RECEIVED: 21-Apr-2022 DATE OF ISSUE: 26-Apr-2022

SPECIFIC COMMENTS

Equipment information (Brand name, Model No., Serial No. and Equipment No.) is provided by client.

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the laboratory or quoted from relevant international standards.

The validity of equipment/ meter performance only applies to the result(s) stated in the report.

Equipment Type: Multifunctional Meter Service Nature: Performance Check

Scope: Conductivity, Dissolved Oxygen, pH Value, Turbidity, Salinity and Temperature

Brand Name/ Model No.: [YSI]/ [Professional DSS]

Serial No./ Equipment No.: [20]101862/15H103928]/ [EQW018]

Date of Calibration: 26-April-2022

GENERAL COMMENTS

This report superseded any previous report(s) with same work order number.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganics

 $This\ report\ may\ not\ be\ reproduced\ except\ with\ prior\ written\ approval\ from\ ALS\ Technichem\ (HK)\ Pty\ Ltd.$

WORK ORDER: HK2214108

SUB-BATCH: 0

DATE OF ISSUE: 26-Apr-2022

CLIENT: ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[YSI]/ [Professional DSS]

Serial No./ Equipment No.:

[20J101862/15H103928]/[EQW018]

Date of Calibration: 26-April-2022 Date of Next Calibration: 26-July-2022

PARAMETERS:

Conductivity Method Ref: APHA (21st edition), 2510B

Expected Reading (µS/cm)	Displayed Reading (µS/cm)	Tolerance (%)
146.9	153.1	+4.2
6667	6431	-3.5
12890	12657	-1.8
58670	56091	-4.4
	Tolerance Limit (%)	±10.0

Dissolved Oxygen

Method Ref: APHA (21st edition), 45000: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.30	3.47	+0.17
5.56	5.67	+0.11
8.18	8.20	+0.02
	Tolerance Limit (mg/L)	±0.20

pH Value Method Ref: APHA (21st edition), 4500H: B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)
4.0	3.83	-0.17
7.0	7.08	+0.08
10.0	9.97	-0.03
	Tolerance Limit (pH unit)	±0.20

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganics

WORK ORDER: HK2214108

SUB-BATCH: 0

DATE OF ISSUE: 26-Apr-2022

CLIENT: ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[YSI]/ [Professional DSS]

Serial No./ Equipment No.:

[20J101862/15H103928]/[EQW018]

Date of Calibration: 26-April-2022 Date of Next Calibration: 26-July-2022

PARAMETERS:

Turbidity Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.00	
4	4.13	+3.3
40	41.69	+4.2
80	76.20	-4.8
400	403.20	+0.8
800	764.91	-4.4
	Tolerance Limit (%)	±10.0

Salinity Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	
10	10.03	+0.3
20	20.38	+1.9
30	30.29	+1.0
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu, Iris

Assistant Manager - Inorganics

WORK ORDER: HK2214108

SUB-BATCH: 0

DATE OF ISSUE: 26-Apr-2022

CLIENT: ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING

Equipment Type: Multifunctional Meter

Brand Name/ Model No.:

[YSI]/ [Professional DSS]

Serial No./ Equipment No.:

[20J101862/15H103928]/[EQW018]

Date of Calibration: 26-April-2022 Date of Next Calibration: 26-July-2022

PARAMETERS:

Temperature Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
7.5	8.2	+0.7
23.5	22.4	-1.1
38.0	36.5	-1.5
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

16:3

Ms. Lin Wai Yu, Iris Assistant Manager - Inorganics

Groundwater Monitoring Results

Table F8.1 Groundwater Monitoring Results

Parameters	Units	MWX-1	MWX-2	MWX-3	MWX-4	MWX-5	MWX-6	MWX-7	MWX-8	MWX-9	MWX-10	MWX-11	MWX-12	MWX-13	MWX-14
Water Level	mPD	3.5	3.63	3.7	3.73	3.76	3.76	3.37	3.62	4.59	4.74	4.73	7.17	38.35	46.08
Bicarbonate Alkalinity as CaCO3	mg/L	107	276	163	<1	36	<1	<1	<1	171	173	122	56	16	11
Carbonate Alkalinity as CaCO3	mg/L	<1	<1	<1	61	22	103	91	82	<1	<1	<1	<1	<1	<1
Total Alkalinity as CaCO3	mg/L	107	276	163	68	58	170	141	116	171	173	122	56	16	11
pH Value	pH Unit	8	7.9	7.8	10.3	9.4	11.3	11.1	10.7	8.1	7.6	7.6	6.9	5.7	5.3
Electrical Conductivity	μS/cm	702	2060	1080	681	883	1300	1300	3140	14600	1380	433	319	92	120
Ammonia as N	mg/L	0.26	0.21	1.12	2	0.55	3.25	4.85	14	0.63	< 0.01	0.02	0.01	< 0.01	< 0.01
Chloride	mg/L	101	338	154	108	127	169	195	1020	4130	228	36	18	14	22
Nitrite as N	mg/L	< 0.01	0.01	< 0.01	< 0.01	0.02	< 0.01	< 0.01	< 0.01	0.01	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01
Reactive Phosphorus as P	mg/L	< 0.01	0.07	0.02	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	0.05	0.02	< 0.01	0.03	< 0.01	< 0.01
Sulphate as SO4 - Turbidimetric	mg/L	70	209	132	81	135	132	138	42	795	154	45	68	3	4
Sulphide as S2	mg/L	0.1	< 0.1	< 0.1	3.4	< 0.1	3.6	5.1	13	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1	< 0.1
Total Kjeldahl Nitrogen as N	mg/L	0.4	0.4	1.3	2	0.9	3.7	5.1	14.2	0.9	0.1	0.1	< 0.1	< 0.1	< 0.1
Nitrate as N	mg/L	< 0.01	0.78	0.06	< 0.01	< 0.01	< 0.01	< 0.01	< 0.01	0.06	< 0.01	0.17	< 0.01	0.13	0.18
Total Nitrogen as N	mg/L	0.4	1.2	1.4	2	0.9	3.7	5.1	14.2	1	0.1	0.3	< 0.1	0.2	0.2
Boron	μg/L	110	290	190	220	220	200	220	540	2690	160	90	20	20	20
Calcium	mg/L	42.8	78.4	91.3	18.5	18.2	36.4	23.9	71.3	111	104	45.7	28.6	0.92	1.4
Mercury	μg/L	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20
Magnesium	mg/L	4.95	75.2	6.42	1.32	0.31	< 0.05	< 0.05	0.13	228	11.1	2.54	4.58	1	1.2
Sodium	mg/L	73	224	106	92.1	123	161	186	582	2460	156	33.2	24	13	16.2
Iron	mg/L	0.05	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	0.32	< 0.04	< 0.04
Potassium	mg/L	17.1	22.6	27.1	27.4	47.8	62.4	53.1	4.06	11.8	12.4	7.43	2.93	3.81	4.16
Cadmium	μg/L	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2	< 0.2
Chromium	μg/L	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1
Copper	μg/L	<1	<1	<1	<1	2	<1	<1	<1	<1	1	2	<1	<1	<1
Lead	μg/L	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1	<1
Manganese	μg/L	517	366	936	2	3	<1	<1	<1	229	1490	9	738	17	16
Nickel	μg/L	<1	<1	<1	<1	<1	1	2	<1	<1	<1	<1	<1	<1	<1
Zinc	μg/L	<10	<10	<10	<10	<10	<10	<10	<10	<10	<10	<10	13	10	12
Biochemical Oxygen Demand	mg/L	<2	<2	2	<2	<2	3	<2	13	<2	<2	<2	<2	<2	<2
Chemical Oxygen Demand	mg/L	26	6	15	16	12	32	35	42	60	15	9	<2	<2	6
Total Organic Carbon	mg/L	6	2	9	7	8	11	14	12	6	6	5	1	1	4

Investigation Report of Environmental Quality Limit Exceedance

Investigation Report of Environmental Quality Limit Exceedance

Project	South East New Territories (SENT) Landfill Extension
Date	8 July 2022
Time	10:45
Monitoring Location	DP4
Parameter	Surface Water (Suspended Solids (SS))
Limit Level	>20 mg/L
Measured Level	26.3 mg /L
Possible reason	From the on-site rainfall record of July 2022, heavy rainfall events were recorded on 1, 2 and 6 July 2022 before the sampling event. Amber rainstorm warning signal was also issued by the Hong Kong Observatory on 1 July 2022.
	No works which may lead to potential SS increase (e.g. active stockpiling and excavation works) was conducted in the vicinity of surface water channel leading to DP4 on the sampling day based on on-site observations and construction activities described by the Contractor.
	Site surface runoff at DP4 channel was treated by the Wetsep prior to discharge. During the sampling event, no raining was recorded and no other sources (e.g. other project sites) was identified in the vicinity of surface water channel leading to DP4 which might cause the SS exceedance at DP4. Contaminated runoff from the unpaved areas during the previous rainfall events could be the potential source of SS contributing to the exceedance. The SS exceedance at DP4 was therefore deemed to Project-related activities.
	It should be noted that although the measured SS level exceeded the limit level of the EM&A programme, it is still within the WPCO effluent discharge limit of SS for the Junk Bay Water Control Zone (30 mg/L). The discharge of surface water with this SS level from DP4 will not cause adverse water quality impact to the Junk Bay Water Control Zone.
Action Taken / Action to be Taken	Weekly surface water quality monitoring (SS) shall be continued at DP4 until no exceedance of Limit Level in accordance with Table 4.5b of the updated EM&A Manual.
	Examination of environmental performance of the Project will be continued during the weekly inspections. The Contractor is reminded to implement relevant and appropriate mitigation measures according to the updated EM&A Manual to avoid any exceedance of the Action and Limit Levels.
	In addition, the Contractor shall review the efficiency of the Wetsep near sediment trap and monitor the Wetsep operation regularly to


	ensure it is functioning properly at all times.
Remarks	-

Prepared by: Abbey Lau
Designation: Environmental Team
Date: 19 July 2022

Annex G

Landfill Gas

Landfill Gas Monitoring
Locations for Service Voids,
Utilities and Manholes
along the Site Boundary and
Within the SENTX Site

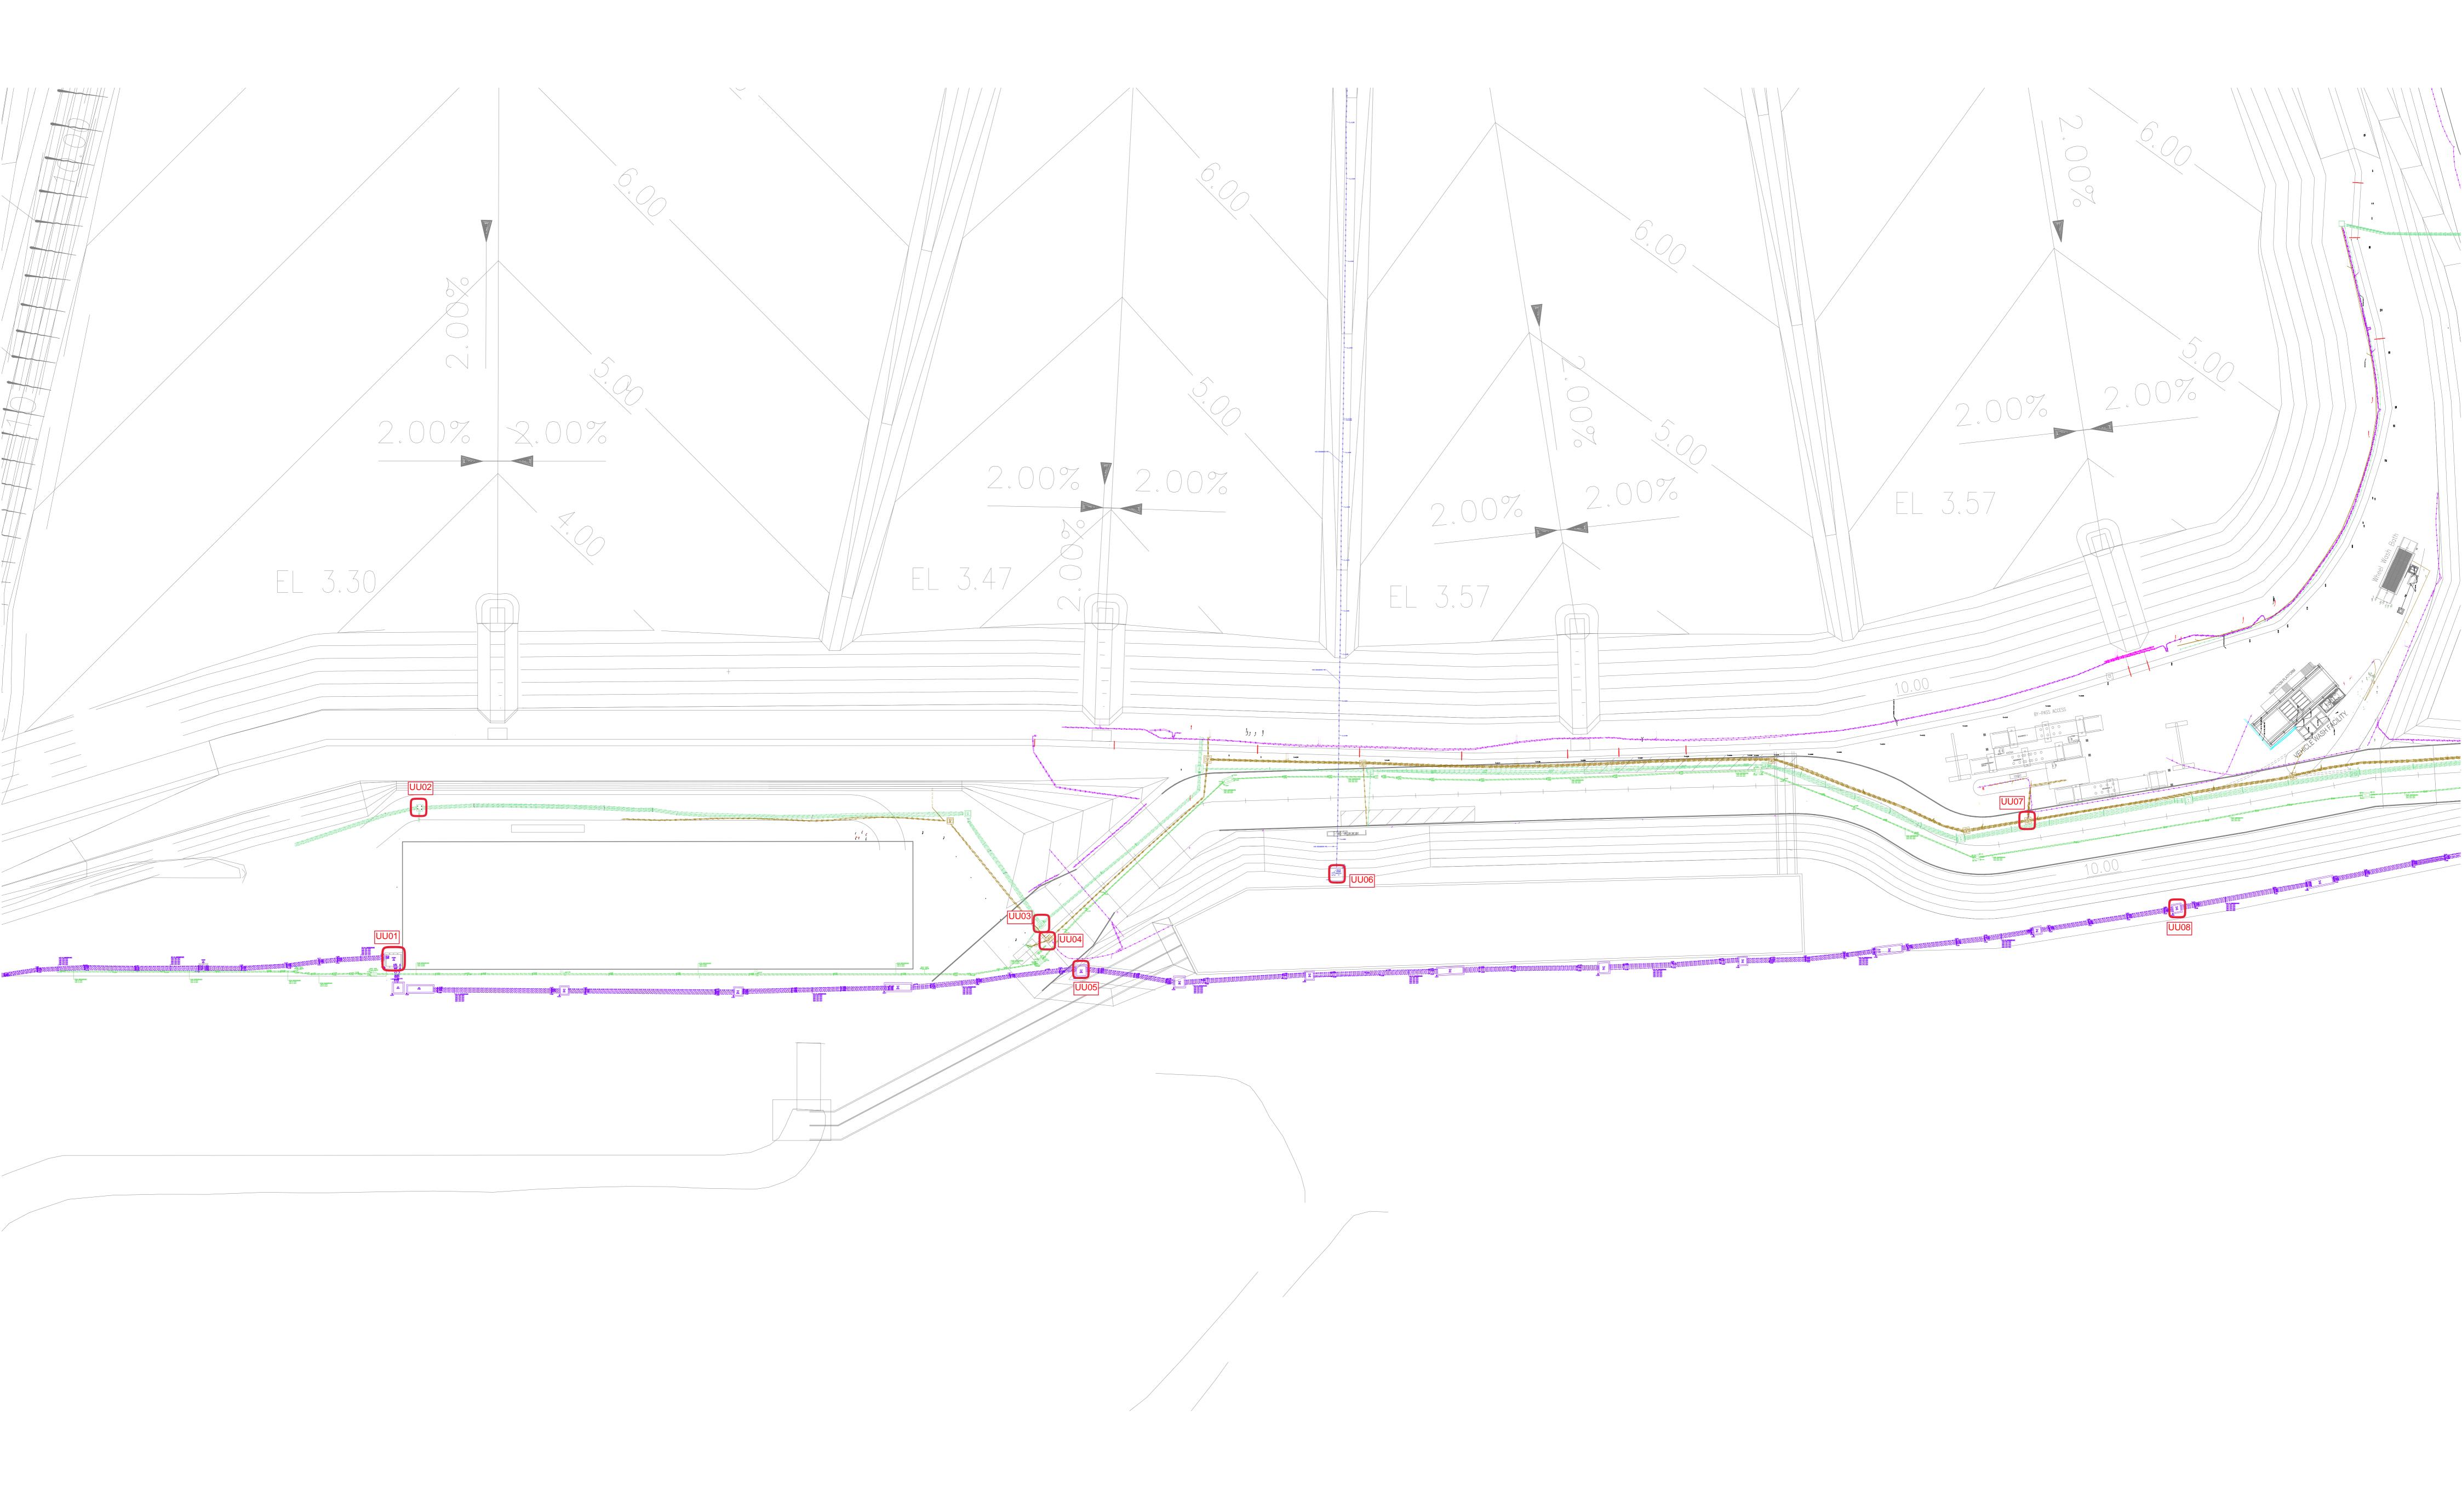



Calibration Certificates for Landfill Gas Monitoring Equipment



ALS Technichem (HK) Pty Ltd

11/F, Chung Shun Knitting Centre 1-3 Wing Yip Street, Kwai Chung N.T., Hong Kong

T: +852 2610 1044 | F: +852 2610 2021

CERTIFICATE OF ANALYSIS

CONTACT: MR IVAN LEUNG WORK ORDER: HK2224153

CLIENT: ALS TECHNICHEM (HK) PTY LTD

ADDRESS: 11/F., CHUNG SHUN KNITTING CENTRE, SUB BATCH: 0

1-3 WING YIP STREET, KWAI CHUNG, N.T. LABORATORY: HONG KONG

DATE RECEIVED: 23-Jun-2022 DATE OF ISSUE: 05-Jul-2022

SPECIFIC COMMENTS

Equipment information (Brand name, Model No., Serial No. and Equipment No.) is provided by client. The performance of the equipment stated in this report is checked with independent reference material and results are compared against a calibrated secondary source.

The "Instrument Specification" quoted is the acceptance criteria applicable for similar equipment used by the laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principles as practised by the laboratory or quoted from relevant international standards.

The validity of equipment/ meter performance only applies to the result(s) stated in the report.

Equipment Type: Landfill Gas Analyser Service Nature: Performance Check

Scope: Carbon dioxide, Methane and Oxygen

Brand Name/ Model No.: GA5000

Serial No./Equipment No.: G507306 (HK1935)
Date of Calibration: 05 July, 2022

GENERAL COMMENTS

This report superseded any previous report(s) with same work order number.

Ms Chan Ka Yu, Karen Manager - Organics

 $This\ report\ may\ not\ be\ reproduced\ except\ with\ prior\ written\ approval\ from\ ALS\ Technichem\ (HK)\ Pty\ Ltd.$

Page 1 of 2

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order: HK2224153

Sub-Batch: 0

Client: ALS TECHNICHEM (HK) PTY LTD

Date of Issue: 05-Jul-2022

Equipment Type: Landfill Gas Analyser

Brand Name/ Model No.:

Equipment No.:

GA5000

Serial No./

G507306 (HK1935)

Date of Calibration: 05 July, 2022

Date of next Calibration: 05 August, 2022

Parameters:

Methane

Calibrated Gas Standard, %	Monitor Readout, %	% error	Instrument Specification, %
0.0 (Nitrogen)	0.0	0.0	± 0.3
1.0	1.0	0.0	± 0.3
10.0	10.0	0.0	± 0.5

Carbon Dioxide

Calibrated Gas Standard, %	Monitor Readout, %	% error	Instrument Specification, %
0.0 (Nitrogen)	0.0	0.0	± 0.3
1.0	1.0	0.0	± 0.3
10.0	10.0	0.0	± 0.5

Oxygen

Calibrated Gas Standard, %	Monitor Readout, %	% error	Instrument Specification, %
0.0 (Nitrogen)	0.0	0.0	± 1.0
23.5	24.0	0.5	± 1.0

Ms Chan Ka Yu, Karen Manager - Organics

Landfill Gas Monitoring Results

Table G3.1 Landfill Gas Monitoring Results at Perimeter LFG Monitoring Wells

Location	Water Level (mPD)	Methane (% (v/v))	Carbon Dioxide (% (v/v))	Oxygen (% (v/v))
LFG1	2.95	0.0	0.5	17.2
LFG2	2.86	0.0	0.6	17.9
LFG3	3.03	0.0	0.0	19.3
LFG4	2.97	0.0	0.2	18.7
LFG5	3.38	0.0	0.0	19.2
LFG6	2.9	0.0	0.0	19.3
LFG7	3.3	0.0	0.0	19.2
LFG8	3.19	0.0	0.0	19.4
LFG9	3.07	0.0	0.0	19.4
LFG10	2.99	0.0	0.0	19.4
LFG11	3.27	0.0	0.0	19.5
LFG12	3.16	0.0	0.0	19.5
LFG13	2.8	0.0	0.0	19.4
LFG14	2.64	0.0	0.0	19.3
LFG15	2.98	0.0	0.0	19.4
LFG16	3.07	0.0	0.0	19.3
LFG17	3.04	0.0	0.0	19.1
LFG18	3.82	0.0	0.0	19.1
LFG19	4.21	0.0	0.0	19.1
LFG20	4.03	0.0	0.0	19.0
LFG21	4.05	0.0	0.0	19.0
LFG22	3.65	0.0	0.0	19.0
LFG23	12.76	0.0	0.4	18.4
LFG24	6.65	0.0	0.0	18.8
GP1	Probe bent	0.2	3.4	12.5
GP2 (shallow)	Probe bent	0.1	0.0	19.6
GP2 (deep)	Probe bent	0.3	0.1	19.5
GP3 (shallow)	Probe bent	0.0	0.4	18.8
GP3 (deep)	Probe bent	0.0	0.5	19.5
GP4 (shallow)	Probe bent	0.0	0.5	18.7
GP4 (deep)	Probe bent	0.0	0.2	19.1
GP5 (shallow)	Probe bent	0.0	5.0	12.8
GP5 (deep)	42.78	0.0	0.1	18.9
GP6	39.99	0.0	1.5	17.3
GP7	36.95	0.0	1.4	15.7
GP12	2.38	0.0	0.0	19.4
GP15	2.97	0.0	0.0	19.6
P7	2.89	0.0	0.0	19.4
P8	3.01	0.0	0.0	19.5
P9	2.89	0.0	0.0	19.6

Table G3.2 Landfill Gas Monitoring Results at Service Voids, Utilities Pits and Manholes

Location	Methane (% (v/v))	(% (v/v)) Carbon Dioxide Oxyge (% (v/v))	
UU01	0.0	0.0	19.8
UU02	0.0	0.0	20.1
UU03	0.0	0.0	20.2
UU04	0.0	0.0	19.8
UU05	0.0	0.0	19.8
UU06	0.0	0.0	20.0
UU07	0.0	0.0	19.7
UU08	0.0	0.0	20.4
UU09	0.0	0.0	19.4
UU10	0.0	0.0	19.0
UU11	0.0	0.0	20.7
UU12	Voided due to latest	site programme and on-	going operation work
UU13	0.0	0.0	20.9
UU14	0.0	0.0	21.0
UU15	0.0	0.0	19.5
UU16	0.0	0.0	18.5
UU17	Voided due to latest	site programme and on-	going operation work
UU18	0.1	0.0	20.9
UU19	0.0	0.0	19.8
UU20	0.0	0.0	18.2
UU21	0.0	0.0	18.4
UU22	0.0	0.0	19.0
UU23	0.0	0.0	19.5
UU24	0.0	0.0	20.1
UU25	0.0	0.0	20.3
UU26	0.0	0.0	18.6
UU27	0.0	0.0	20.4
UU28	0.0	0.0	20.8

Event and Action Plan for Landfill Gas Monitoring

Annex G4 Event and Action Plan for Landfill Gas Monitoring

Event	Action					
	ET	IEC	Contractor			
Limit Level being exceeded for field monitoring at the perimeter monitoring wells	 Investigate the cause(s) of exceedance Prepare the Notification of Exceedance within 24 hours Check monitoring data, all plant, equipment and the Contractor's working methods Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Increase the monitoring frequency to daily if exceedance is due to the Project for monitoring wells in the areas where there is development within 250m of the SENTX Site Boundary and to weekly for other monitoring wells, until no exceedance of limit level 	 Verify the Notification of Exceedance Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Repeat field measurement to confirm findings Check the performance of landfill gas management system Rectify unacceptable practice Discuss with the ET and IEC and submit proposals for remedial measures to IEC Implement the agreed proposals Amend proposal if appropriate 			
Limit Level being exceeded for the bulk gas sampling at the perimeter monitoring wells	 Check and compare the results of field monitoring and laboratory analyse of bulk samples If the results of field monitoring also show exceedance, the action(s) for limit level being exceeded for field monitoring would have been triggered If the results of field monitoring does not show exceedance, the sampling procedures should be checked and if deems necessary, to repeat the monitoring and recalibrate the portable monitoring instruments Notify the above findings to Contractor and IEC 		• Nil			

ENVIRONMENTAL RESOURCES MANAGEMENT

GREEN VALLEY LANDFILL LTD.

Event	Action					
	ET	IEC	Contractor			
Limit Level being exceeded at the permanent gas monitoring system	 Investigate the cause(s) of exceedance Prepare the Notification of Exceedance within 24 hours Check the methane gas level at the perimeter monitoring wells, manholes or utilities duct Check monitoring data, all plant, equipment and the Contractor's working methods Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented 	 Verify the Notification of Exceedance Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Evacuate all staff in the concerned building Open the doors and window of all rooms on the ground floor Do not allow staff to go back to the room if methane level is higher than 1% gas Check the performance of the landfill gas management system Rectify unacceptable practice Consider changes of working methods Discuss with the ET and IEC and submit proposals for remedial measures to IEC Implement the agreed proposals Amend proposal if appropriate 			
Limit Level being exceeded during surface emission monitoring	 Repeat the measurement to confirm findings Investigate the cause(s) of exceedance Prepare the Notification of Exceedance within 24 hours Check monitoring data, all plant, equipment and the Contractor's working methods Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Increase the monitoring frequency to monthly if exceedance is due to the Project until no exceedance of limit level 	 Verify the Notification of Exceedance Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Check landfill gas management system Rectify unacceptable practice Consider changes of working methods Discuss with the ET and IEC and submit proposals for remedial measures to IEC Implement the agreed proposals Amend proposal if appropriate 			

Event	Action					
	ET	IEC	Contractor			
Limit Level being exceeded at the service voids, utilities pits, manholes and location of vegetation stress	 Repeat the measurement to confirm findings Investigate the cause(s) of exceedance Prepare the Notification of Exceedance within 24 hours Check monitoring data, all plant, equipment and the Contractor's working methods Inform Contractor, IEC, Project Proponent and EPD (EIAO Authority) whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Increase the monitoring frequency to weekly if exceedance is due to the Project until no exceedance of limit level 	 Verify the Notification of Exceedance Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures the effectiveness of the implemented remedial measures 	 Check landfill gas management system Rectify unacceptable practice Discuss with the ET and IEC and submit proposals for remedial measures to IEC Implement the agreed proposals Amend proposal if appropriate 			

Annex H

Cumulative Statistics on Exceedances, Environmental Complaints, Notification of Summons and Status of Prosecutions

 Table H1
 Cumulative Statistics on Exceedances

		Total No. recorded in this reporting period	Total No. recorded since project
			commencement
Air Quality (Dust)	Action	0	0
	Limit	2	3
Air Quality (Odour)	Action	0	0
	Limit	0	0
Air Quality (Emissions of Thermal	Limit	0	0
Oxidiser)			
Air Quality (Emissions of Landfill	Limit	0	1
Gas Flare)			
Air Quality (Emissions of Landfill	Limit	0	0
Gas Generator)			
Noise	Action	0	0
	Limit	0	0
Water Quality (Surface Water)	Limit	1	60
Water Quality (Leachate)	Limit	0	0
Water Quality (Groundwater)	Limit	0	7
Landfill Gas (Perimeter Landfill Gas	Limit	0	1
Monitoring Wells)			
Landfill Gas (Service Void, Utilities	Limit	0	0
and Manholes)			
Landfill Gas (Permanent Gas	Limit	0	0
Monitoring System)			

Table H2 Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Reporting Period	Cumulative Statistics			
_	Complaints	Notifications of Summons	Prosecutions	
This Reporting Period (1 – 31 July 2022)	0	0	0	
Total no. received since project commencement	1	0	0	

Annex I

Monitoring Schedule for the Next Reporting Period

South East New Territories (SENT) Landfill Extension EM&A Impact Monitoring Schedule during Operation/ Restoration Phase

<u>August 2022</u>

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	Noise Monitoring	2 Leachate Monitoring	Leachate Monitoring	4 Dust Monitoring	5 Service Void LFG Monitoring	6
	Leachate Monitoring					
7	8 VOCs Monitoring	9 Stack Monitoring	Dust Monitoring	Noise Monitoring	12 Perimeter LFG Monitoring	13
	Stack Monitoring				Perimeter LFG Bulk Gas Sampling	
14	15 Flammable Gas Monitoring	16 Dust Monitoring	17 Groundwater Monitoring	18	19	20
	Groundwater Monitoring	Dust Wolltoring	Noise Monitoring			
21	22 Dust Monitoring	23 Noise Monitoring	24	25	26	27
	Odour Monitoring	Surface Water Monitoring				
Dust Monitoring	Noise Monitoring	30	31			
