Route 8 (previously known as Route 9) between Cheung Sha Wan & Sha Tin

Contract No. HY/2003/10 - Environmental Team for Lai Chi Kok Viaduct and Eagle's Nest Tunnel

Monthly EM&A Report
Part II – Eagle's Nest Tunnel & Associated Works
(Version 1.0)
November 2007

Approved By

(Environmental Team Leader)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties.

CINOTECH CONSULTANTS LTD

Room 1710, Technology Parke, 18 On Lai Street, Shatin, NT, Hong Kong Tel: (852) 2151 2083 Fax: (852) 3107 1388 Email: info@cinotech.com.hk

TABLE OF CONTENTS

EX	ECUTIVE SUMMARY	I
	Introduction Environmental Monitoring and Audit Works Environmental Licenses and Permits Key Information in the Reporting Month	1
1.	INTRODUCTION	3
	Background Project Organizations Construction Programme Summary of EM&A Requirements	4 4
2.	AIR QUALITY	6
	Monitoring Requirements Monitoring Locations Monitoring Equipment Monitoring Parameters, Frequency and Duration Monitoring Methodology and QA/QC Procedure Results and Observations	6 6 7
3.	NOISE	9
	Monitoring Requirements Monitoring Locations Monitoring Equipment Monitoring Parameters, Frequency and Duration Monitoring Methodology and QA/QC Procedures Maintenance and Calibration Results and Observations	9 10 10 11
4.	ENVIRONMENTAL AUDIT	12
	Site Audits Review of Environmental Monitoring Procedures Status of Environmental Licensing and Permitting Implementation Status of Environmental Mitigation Measures Summary of Exceedances Implementation Status of Event Action Plans Summary of Complaints and Prosecutions	12 12 12 16
5.	FUTURE KEY ISSUES	17
	Key Issues for the Coming Month Monitoring Schedule for the Next Month Construction Program for the Next Month	17
6.	CONCLUSIONS AND RECOMMENDATIONS	19
	Conclusions Recommendations	

LIST OF TABLES

Table I	Summary Table for Events Recorded in the Reporting Month
Table II	Summary Table for Key Information in the Reporting Month
Table 1.1	Key Project Contacts
Table 2.1	Locations for Air Quality Monitoring
Table 2.2	Air Quality Monitoring Equipment
Table 2.3	Impact Dust Monitoring Parameters, Frequency and Duration
Table 3.1	Noise Monitoring Stations
Table 3.2	Noise Monitoring Equipment
Table 3.3	Noise Monitoring Parameters, Frequency and Duration
Table 4.1	Summary of Environmental Licensing and Permit Status
Table 4.2	Observations and Recommendations of Site Audit
Table 4.3	Observations and Recommendations of Site Audits Followed up for Pervious
	Month for Civil Works

LIST OF FIGURES

Figure 1a	Locations of Monitoring Stations
Figure 1b	Locations of Monitoring Stations

LIST OF APPENDICES

Action and Limit Levels for Air Quality and Noise
Copies of Calibration Certificates
Environmental Monitoring Schedules
Wind Data
1-hour TSP Monitoring Results and Graphical Presentations
24-hour TSP Monitoring Results and Graphical Presentations
Noise Monitoring Results and Graphical Presentations
Summary of Exceedance
Site Audit Summary
Event Action Plans
Environmental Mitigation Implementation Schedule (EMIS)
Construction Programme
Complaint Log

ABBREVIATION AND ACRONYM

AL Levels Action and Limit Levels

E / ER Engineer/Engineer's Representative

EIA Environmental Impact Assessment

EM&A Environmental Monitoring and Audit

EMIS Environmental Mitigation Implementation Schedule

EP Environmental Permit

EPD Environmental Protection Department

ET Environmental Team

HVS High Volume Sampler

IEC Independent Environmental Checker

RE Resident Engineer

RH Relative Humidity

TSP Total Suspended Particulates

TDD Territory Development Department

QA/QC Quality Assurance / Quality Control

SLM Sound Level Meter

WMP Waste Management Plan

EXECUTIVE SUMMARY

Introduction

- This is the 48th monthly Environmental Monitoring and Audit (EM&A) Report prepared by Cinotech Consultants Limited for the "Route 8 (previously known as Route 9) between Cheung Sha Wan & Sha Tin, Lai Chi Kok Viaduct & Eagle's Nest Tunnel". This report documents the findings of EM&A Works conducted in November 2007 for Contract No. HY/2003/02, Eagle's Nest Tunnel and Associated Works (the Project).
- The major site activities for civil works undertaken in the reporting month included:
 - Cladding and Hand Rail Installation;
 - Tunnel Ventilation System (T&C);
 - Plumbing & Drainage;
 - Mechanical Ventilation Air Conditioning and T&C;
 - Road works:
 - Metal curtain and mesh cladding;
 - Earth works:
 - Cat ladder for vent shaft;
 - Upper roof railing;
 - Cut/ fill slope at SP-S2;
 - Metal cladding on footbridge, false and external metal ceiling and signages at Toll Plaza's structures & Administration Building; and
 - Haul road diversion, step channel, irrigation pipe and system, WSD access and the works on u-channel at Butterfly Valley.
- The major site activities for Traffic Control and Surveillance System (TCSS) works undertaken in the reporting month included:
 - Equipment Cabinet Installation;
 - Equipment Cabinet Termination;
 - Cable Termination for Field Equipment; and
 - SCT for PA, TCSS equipments and cables and in-house equipments in ELV room.

Environmental Monitoring and Audit Works

- Environmental monitoring and audit works for the Project was performed regularly as stipulated in the EM&A Manual and the results were checked and reviewed. Site audits were conducted once per week. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.
 - Summary of events and actions taken in the reporting month is tabulated in **Table I**.

Table I Summary of Events Recorded in the Reporting Month

Parameter	No. of	Events	No. of Events	Action Taken	
1 arameter	Action Level	Limit Level	Due to the Project	Action Tuken	
1-hr TSP	0	0	0	N/A	
24-hr TSP	0	0	0	N/A	
Noise	0	0	0	N/A	

Environmental Licenses and Permits

• Licenses/Permits granted to the Project include the Environmental Permit (EP) for the Project, Registration of Chemical Waste Producer (RCWP), Construction Noise Permits (CNPs) and Water Discharge Licenses (WDLs). Three new CNPs were issued to the Project by EPD in the reporting month.

Key Information in the Reporting Month

• Summary of key information in this reporting month is tabulated in **Table II**.

Table II Summary Table for Key Information in the Reporting Month

Event	Event Details		Action Taken	Status	Remark	
Event	Number Nature		Action Taken	Status	Kemark	
Complaint received	0		N/A	N/A		
Changes to the assumptions and key construction / operation activities recorded	0		N/A	N/A		
Status of submissions under EP	0		N/A	N/A		
Notifications of any summons & prosecutions received	0		N/A	N/A		

Future Key Issues:

Major site activities for civil works in the coming months include:

- Cladding and Hand Rail Installation;
- Tunnel Ventilation System and Lighting (T&C);
- Plumbing & Drainage;
- Mechanical Ventilation Air Conditioning and T&C;
- Road and drainage works:
- Metal curtain and mesh cladding;
- Cat ladder for vent shaft;
- Upper roof railing;
- Fencing at Ventilation Building;
- Testing on fire services and lighting:
- Metal cladding on footbridge, painting, fire services, carpet file false and external metal ceiling and signages at Toll Plaza's structures & Administration Building; and
- Haul road diversion, step channel, fill slope at SP-S2, irrigation pipe and system (T&C), u-channel and lighting for noise enclosure at Butterfly Valley.

Major site activities for TCSS works in the coming months include:

- Equipment Cabinet Installation;
- SAT for TCSS equipment; and
- Remedial works for TCSS equipment.

The anticipated environmental issues will be mainly on dust from stockpiles, road works, fill slope and earth works, noise impact from road works and waste/ chemical management from finishing the construction activities.

1. INTRODUCTION

Background

- 1.1 Route 9 (Kowloon Section) (R9K) (hereinafter call the R9K-Project) forms part of the Route 9 between Cheung Sha Wan and Sha Tin (R9-CSWST) project, which will be a new expressway connecting West Kowloon and Sha Tin. It will be the fourth external link between Sha Tin and Kowloon and will form an important link between the northeast New Territories and the west Kowloon, Lantau Island and the western New Territories. R9K is being managed and implemented by the Highways Department (HyD).
- 1.2 The engineering design of R9K is covered under Agreement No. CE 50/98 "Route 9 between Cheung Sha Wan and Sha Tin Design Construction Assignment". The main consultant engaged under Agreement No. CE 50/98 is Maunsell Hyder Joint Venture (MHJV), who acts as the Engineer for the construction contracts. The works of R9K mainly comprise a 1.4km dual 3-lane Lai Chi Kok Viaduct from Lai Wan Interchange to Butterfly Valley; 0.5 km of dual 3-lane at-grade carriageway linking to the 2.1 km dual 3-lane twin-bore Eagle's Nest Tunnel with associated portal buildings; a toll plaza with an administration building located with the Sha Tin valley woodland; a ventilation building and an adit; associated noise barriers, noise enclosures, drainage, slope and landscape works; and electrical and mechanical works for the whole R9-CSWST. The remainder of the R9-CSWST forms the Sha Tin Section (R9S) of the project and is being managed and implemented separately by the Civil Engineering and Development Department (CEDD).
- 1.3 The R9-CSWST project is a Designated Project under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). An environmental impact assessment (EIA) report has been prepared in 1998 for the R9-CSWST project (1998 R9 EIA) to consider the key issues of noise, air quality, water quality, ecological, construction waste, landscape and visual, land use and cultural impacts, and identify possible mitigation measures.
- 1.4 An Updated Final EIA report was subsequently completed in September 1999 for the R9-CSWST project (1999 R9 EIA), to cater for some changes in R9K portion as mentioned in paragraph 1 of the report. The 1999 R9 EIA was endorsed by Environmental Protection Department (EPD) in November 1999. The 1998 R9 EIA and the 1999 R9 EIA (R9 EIA Reports) were included in the EIA register under the EIAO as report no. EIA-135/BC and AEIAR-022/1999 respectively. An Environmental Monitoring and Audit (EM&A) Manuals for each of the R9 EIA Reports (EM&A Manuals) were also included as part of the EIA reports in the register.
- 1.5 Subsequent to the endorsement of the R9 EIA Reports by EPD in November 1999, the project programme was deferred to start in 2002/2003 for completion by 2006/07. The implementation of the project was then separated into the R9S and R9K portion. An Environmental Permit (EP) No. EP-103/2001 was issued on 17 September 2001 for R9K to the HyD as Permit Holder and a varied EP No. EP-103/2001/A was subsequently issued on 20 May 2003 for R9K (R9K EP) to HyD as Permit Holder. A varied EP-103/2001/C was recently issued on 22 July 2005.

- 1.6 The major construction activities of two civil contracts of the R9K project, Contract No. HY/2003/01 entitled "Route 9 Lai Chi Kok Viaduct" and Contract No. HY/2003/02 entitled "Route 9 Eagle's Nest Tunnel and Associated Works", were commenced on 15th December 2003 for completion in April 2007.
- 1.7 "Route 9" was recently re-tiled as "Route 8 (previously known as Route 9)". Cinotech Consultants Limited (Cinotech) was commissioned by HyD to undertake the Environmental Monitoring and Audit works for "Route 8 (previously known as Route 9) between Cheung Sha Wan and Sha Tin Environmental Team (ET) for Lai Chi Kok Viaduct and Eagle's Nest Tunnel (Contract No. HY/2003/10)". Dr. Priscilla CHOY of Cinotech Consultants Ltd. was appointed as the ET Leader under Condition 2.2 of the EP. Mr. Kenneth LUK of CH2M HILL Hong Kong Ltd. was appointed as the IEC under Condition 2.1 of the EP. This is the 48th monthly EM&A report summarizing the EM&A works for the Project in November 2007.

Project Organizations

- 1.8 Different parties with different levels of involvement in the project organization include:
 - Project Proponent Major Works Project Management Office (MWPMO) of Highways Department (HyD)
 - Engineer / Engineer's Representative (E/ER) Maunsell-Hyder Joint Venture (MHJV)
 - Environmental Team (ET) Cinotech Consultants Limited
 - Independent Environmental Checker (IEC) CH2M HILL Hong Kong Ltd
 - Contractor Leighton-Kumagai Joint Venture (LKJV)
 - Engineer's Representative for TCSS works Ove Arup & Partners Hong Kong Limited
 - Contractor for TCSS works Delcan-Imtech-Gtech Joint Venture
- 1.9 The responsibilities of respective parties are detailed in Section 1.8.3 of the EM&A Manual (1999) of the Project.
- 1.10 The key contacts of the Project are shown in **Table 1.1**.

Construction Programme

The major site activities for civil works undertaken in the reporting month included Cladding & Hand Rail Installation, Tunnel Ventilation System and T&C, Plumping & Drainage, Mechanical Ventilation Air Conditioning and T&C, Road Works, Metal Curtain & Mesh Cladding, Earth Works, Cat Ladder for Vent Shaft, Upper roof Railing, Cut/fill Slope at SP-S2, Metal Cladding on Footbridge, False and External Metal Ceiling, Signages at Toll Plaza's structures & Administration Building, Haul Road Diversion, Step Channel, Irrigation Pipe and System, WSD Access and the works on U-channel at Butterfly Valley.

- 1.11 The major site activities for TCSS works undertaken in the reporting month included:
 - Cable Laying;
 - Equipment Cabinet Installation;
 - Equipment Cabinet Termination;
 - o Cable Termination for Field Equipment; and
 - SCT and SAT.

Phone **Party** Role Name **Position** Fax No. No. Mr. Kroc Leung SE2/R8K 2762 3662 HyD Permit Holder 2714 5198 Mr. George Law E4/R8K 2762 3675 Engineer Mr. Conrad Ng Project Manager 2605 6262 2691 2649 Mr. Peter Poon CRE 3552 2500 **MHJV** Engineer's 2743 9200 Mr. Eric Wong **RE (S & EP)** 3552 2551 Representative Ms. Sammie Chan TO (EN) 3552 2605 ET Leader Dr. Priscilla Choy 2151 2089 Environmental Mr. Grace Wong Audit Team Leader 2151 2095 Cinotech 3107 1388 Team Monitoring Team Mr. Henry Leung 2151 2087 Leader Independent Independent Mr. Kenneth Luk 2507 2209 Environmental Checker CH2M Environmental 2507 2293 Assistant Independent Checker Mr. Roy Leung 2872 2931 **Environmental Checker** Mr. Ray Brewster **Project Director** 9092 6128 LKJV Contractor 2743 1600 Mr. Danny Cheng QA/E Manager 3552 2113 Engineer's Mr. Donald Leung RE 2436 7489 **ARUP** Representative 2436 1803 ARE Mr. Daniel So 2436 7435 (TCSS) Contractor **DIGJV** Ms. Joyce Chan Quality Manager 2123 0845 2123 0889 (TCSS) **Enquiries Hotline** 3552 2226 Complaint Hotline 3552 2380

Table 1.1 Key Project Contacts

Summary of EM&A Requirements

- 1.12 The EM&A programme requires construction phase monitoring for air quality and construction noise, and environmental site audit. The EM&A requirements for each parameter are described in the following sections, including:
 - All monitoring parameters;
 - Action and Limit levels for all environmental parameters:
 - Event / Action Plans:
 - Environmental mitigation measures, as recommended in the project EIA study final report; and
 - Environmental requirements in contract documents.
- 1.13 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 4 of this report.
- 1.14 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the required monitoring parameters, namely dust and noise levels and audit works for the Project in the reporting month.

2. AIR QUALITY

Monitoring Requirements

2.1 Monitoring of 1-hour and 24-hour TSP were conducted to monitor the air quality. The established Action/Limit Levels for the environmental monitoring works were shown in **Appendix A**.

Monitoring Locations

2.2 Three designated monitoring stations, AM1, AM3 and AM4 were selected for impact dust monitoring for the Project. **Table 2.1** describes the air quality monitoring locations, which are also depicted in **Figure 1a** and **1b**.

Table 2.1 Locations for Air Quality Monitoring

Station	Description	Location	
AM1 ⁽¹⁾ Yew Chung International School / PLK Choi Kai Yau School		Rooftop	
AM3	Slope no. 07SW-D/FR4 near Garden Villa	On Ground	
AM4	Government Quarters	Ground Floor ⁽²⁾	

Note: ⁽¹⁾ Yew Chung International School / PLK Choi Kai Yau School had ceased operated and been demolished since February 2007. The air monitoring at AM1 has been suspended since February 2007, as approved by EPD on 26th April 2007.

Monitoring Equipment

2.3 **Table 2.2** summarizes the equipment used in the impact air monitoring programme. Copies of calibration certificates are attached in **Appendix B**.

Table 2.2 Air Quality Monitoring Equipment

Equipment	Model and Make	Quantity
Calibrator	GMW25; S/N: 1536	1
HVS Sampler	Graseby GMW Model GS2310 High Volume TSP Sampler and associated equipment and shelter	3

Monitoring Parameters, Frequency and Duration

2.4 **Table 2.3** summarizes the monitoring parameters and frequencies of impact dust monitoring for the whole construction period. The air quality monitoring schedule for the reporting period is shown in **Appendix C**.

⁽²⁾ The HVS was installed on the ground floor, which is close to the refuse collection station of the Government Quarters.

 Table 2.3
 Impact Dust Monitoring Parameters, Frequency and Duration

Parameters	Frequency
1-hr TSP	Three times / 6 days
24-hr TSP	Once / 6 days

Monitoring Methodology and QA/QC Procedure

Instrumentation

2.5 Graseby GMW Model GS2310 TSP High Volume Sampler (HVS) was employed for 1-hour & 24-hour TSP monitoring. The sampler was composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complied with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50). Moreover, the HVS also met all the requirements in Sections 2.2 – 2.4 of the Updated EM&A Manual (1999).

Operating/Analytical Procedures

- 2.6 Operating/analytical procedures for the operation of HVS were as follows:
 - A horizontal platform was provided with appropriate support to secure the samplers against gusty wind.
 - No two samplers were placed less than 2 meters apart.
 - The distance between the sampler and an obstacle, such as buildings, was at least twice the height that the obstacle protrudes above the sampler.
 - A minimum of 2 meters of separation from walls, parapets and penthouses was required for rooftop samples.
 - A minimum of 2 meters separation from any supporting structure, measured horizontally was required.
 - No furnaces or incineration flues were nearby.
 - Airflow around the sampler was unrestricted.
 - The sampler was more than 20 meters from the drip line.
 - Any wire fence and gate, to protect the sampler, should not cause any obstruction during monitoring.
- 2.7 Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 1.1 m³/min. and 1.4 m³/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50. For TSP sampling, fiberglass filters (G810) were used.
- 2.8 The power supply was checked to ensure the sampler worked properly. On sampling, the sampler was operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air monitoring station.
- 2.9 The filter holding frame was then removed by loosening the four nuts and a weighted and conditioned filter was carefully centered with the stamped number upwards, on a supporting screen.

- 2.10 The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- 2.11 The shelter lid was closed and secured with the aluminum strip. The timer was then programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number). After sampling, the filter was removed and sent to the laboratory for weighing. The elapsed time was also recorded.
- 2.12 Before weighing, all filters were equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than ± 3 °C; the relative humidity (RH) should be < 50% and not vary by more than ± 5 %. A convenient working RH is 40%.

Maintenance/Calibration

- 2.13 The following maintenance/calibration was required for the HVS:
 - The high volume motors and their accessories were properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking were made to ensure that the equipment and necessary power supply are in good working condition.
 - High volume samplers were calibrated at bi-monthly intervals using GMW-25 Calibration Kit throughout all stages of the air quality monitoring.

Results and Observations

- 2.14 All TSP monitoring was conducted as scheduled in the reporting month.
- 2.15 No Action/Limit Level exceedance for both 1-hour TSP and 24-hour TSP was recorded in the reporting month.
- 2.16 Wind data monitoring equipment has been installed in Shatin Heights for logging wind speed and wind direction. These wind data are summarized in Appendix D.
- 2.17 The monitoring data and graphical presentations of 1-hour and 24-hour TSP monitoring results are shown in Appendices E and F, respectively.

3. NOISE

Monitoring Requirements

- 3.1 Monitoring and audit of construction noise levels is required to be conducted, in accordance with the EM&A Manual, to ensure that any unacceptable noise impacts could be readily detected and timely appropriate action be undertaken to rectify the situation.
- 3.2 The construction noise levels shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). L_{eq} (30min) shall be used as the monitoring parameter for the time period between 0700-1900 hours on normal weekdays. For all other time periods, L_{eq} (5min) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. As supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.
- 3.3 Three designated noise monitoring stations, namely NM1, NM5 & NM6 were selected for impact monitoring in accordance to the EM&A manual (1999) and the subsequent EPD approval of the relocations.
- 3.4 Noise monitoring is also required to be conducted at station NM7 in accordance with the EM&A Manual (1998). The noise monitoring at the station is required to be conducted under CEDD's construction Contract No. ST 89/02 "Sha Tin Heights Tunnel and Approaches" in accordance with the requirement of Environmental Permit No. EP104/2001/A. The impact noise monitoring results at station NM7 are also presented in this report.
- 3.5 **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.

Monitoring Locations

3.6 Noise monitoring was conducted at three designated monitoring stations as summarized in Table 3.1. Figures 1a & 1b show the locations of these stations.

Table 3.1 Noise Monitoring Stations

Monitoring Station	Description	Location	
NM1 ⁽¹⁾	Yew Chung International School / PKL Choi Kai Yau School	Rooftop	
NM5	Villa Carlton	Ground Floor ⁽²⁾	
NM6	Government Quarters	Rooftop of Refuse Collection Station	
NM7	Garden Villa	Rooftop	

Note: ⁽¹⁾ Yew Chung International School / PLK Choi Kai Yau School had ceased operated and been demolished since February 2007. The noise monitoring at NM1 has been suspended since February 2007, as approved by EPD on 26th April 2007.

⁽²⁾ The noise measurement was taken at 2.3m above the ground floor of Villa Carlton, where has a line of sight of the construction site in the opposite.

Monitoring Equipment

3.7 Table 3.2 summarizes the noise monitoring equipment model being used. Copies of calibration certificates are attached in **Appendix B**.

Table 3.2 Noise Monitoring Equipment

Equipment	Model and Make	Qty.
Integrating Sound Level Meter	B&K Model 2238	5
Calibrator	B&K 4231	2
Wind Speed Anemometer	RS232 Integral Vane Digital Anemometer	1

Monitoring Parameters, Frequency and Duration

3.8 Table 3.3 summarizes the monitoring parameters, frequency and total duration of monitoring. The noise monitoring schedule is shown in **Appendix C**.

Table 3.3 Noise Monitoring Parameters, Frequency and Duration

Station	Parameter	Period ¹	Frequency	Measurement
NM1	L ₁₀ (30 min.)dB(A) L ₉₀ (30 min.)dB(A) L _{eq} (30 min.)dB(A)	(a) 0700 1000 hrs. on yyaalidaya		Façade
NM5		(a) 0700-1900 hrs. on weekdays (b) 1900-2300 hrs. on weekdays		Façade
NM6		(c) 0700-2300 hrs. on holidays	week	Free Field
NM7		(d) 2300-0700 hrs on any days		Façade

Note: ¹(b), (c) and (d) will only be conducted if construction works are undertaken during these periods.

Monitoring Methodology and QA/QC Procedures

- The Sound Level Meter was generally set on a tripod at a height of 1.2 m above the ground, depending to the actual monitoring condition.
- For free field measurement (if any), the meter was positioned away from any nearby reflective surfaces. All records for free field noise levels were adjusted with a correction of +3 dB(A).
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:

frequency weightingtime weightingFast

time measurement : 30 minutes / 5 minutes

- Prior to and after each noise measurement, the meter was calibrated using a
 Calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before
 and after measurement was more than 1.0 dB, the measurement would be
 considered invalid and repeat of noise measurement would be required after recalibration or repair of the equipment.
- The wind speed was frequently checked with the portable wind meter.
- At the end of the monitoring period, the $L_{eq},\,L_{90}$ and L_{10} were recorded. In addition,

- site conditions and noise sources were recorded on a standard record sheet.
- Noise measurement was paused during periods of high intrusive noise if possible and observation was recorded when intrusive noise was not avoided.
- Noise monitoring was cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.

Maintenance and Calibration

3.9 The microphone head of the sound level meter and calibrator was cleaned with soft cloth regularly. The meters were sent to the supplier to check and calibrate on a yearly interval.

Results and Observations

- 3.10 Noise monitoring was performed at the three designated locations as scheduled for the daytime period (0700-1900 hours) in this reporting month. Restricted-hour monitoring was also conducted at NM5, NM6 and NM7.
- 3.11 All the Construction Noise Levels (CNLs), except the monitoring (0700-1900 on weekdays) at NM6, reported in this report were adjusted with the corresponding baseline level (i.e. Measured Leq Baseline Leq = Measured CNL), in order to facilitate the interpretation of the noise exceedance.
- 3.12 Noise monitoring results and graphical presentations are shown in **Appendix G**.
- 3.13 No Action/Limit Level exceedance for noise monitoring was recorded in the reporting month.

4. ENVIRONMENTAL AUDIT

Site Audits

- 4.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are provided in **Appendix I**.
- 4.2 Site audits for Civil contract were conducted on 7th, 14th, 21st and 28th November 2007 by ET. A joint site audit for Civil works was conducted on 7th November 2007 with representatives from HyD, IEC, ER, the Contractor and ET while the joint site audit for TCSS works was conducted on 7th November 2007 with the representatives from IEC, ER, the Contractor and ET. No environmental deficiency was recorded for TCSS contract during site inspections.

Review of Environmental Monitoring Procedures

4.3 The monitoring works conducted by the monitoring team were inspected regularly. The following observations have been recorded for the monitoring works:

Air Quality Monitoring

- The monitoring team recorded all observations around the monitoring stations within and outside the construction site.
- The monitoring team recorded the temperature and weather conditions on the monitoring days.

Noise Monitoring

- The monitoring team recorded all observations around the monitoring stations, which might affect the monitoring result.
- Major noise sources were identified and recorded. Other intrusive noise attributing to the result was trimmed off by pausing the monitoring temporarily.

Status of Environmental Licensing and Permitting

4.4 All valid permits/licenses obtained for the Project are summarized in **Table 4.1**. Three new CNPs were issued to the Project by EPD in the reporting month.

Implementation Status of Environmental Mitigation Measures

4.5 According to the Environmental Permit and the EM&A Manuals, the mitigation measures detailed in the documents are required to be implemented. An updated summary of the EMIS is provided in **Appendix K**.

Table 4.1 Summary of Environmental Licensing and Permit Status

Table 4.1 Summary of Environmental Licensing and Permit Status Valid Period Page 19 19 19 19 19 19 19 19 19 19 19 19 19						
Permit No.	From	То	Details	Status		
Environmental Pern		10	<u> </u>			
EP-103/2001/C	22/07/05	N/A	Construction and operation of (a) All civil works (including highways, traffic, geotechnical, drainage, structural, architectural and landscaping works) for the Lai Chi Kok Viaduct, the interchange with Ching Cheung Road, the main road within Butterfly Valley and the Eagle's Nest Tunnel; (b) All E&M works (including ventilation, Traffic Control & Surveillance System (TCSS), toll collection system and lighting) for the whole Route 9 between Cheung Sha Wan and Sha Tin; I The permanent slope works above the northern portal of the Eagle's Nest Tunnel; (d) The architectural works (including fitting out and furnishings) of the portal buildings of the Sha Tin Heights Tunnel.	Valid		
Registration of Cher	nical Waste	Producer	1			
WPN 5213-761- L2595-01	26/01/04	N/A	Regulation for disposal of spent oil and waste batteries arising from construction activities in all project areas.	Valid		
Water Discharge Li	cence					
EP482/261/0327/I	03/05/04	31/05/09	Discharge of industrial trade effluent and effluent arising from construction activities at the construction site at Ventilation Adit on Tai Po Road (behind Shell Filling Station) opposite Pinehill Development Highways.	Valid		
EP482/261/0326/I	01/04/04	30/04/09	Discharge of industrial trade effluent and effluent arising from construction activities at the construction site at Mui Kong Tsuen, Butterfly Valley, Lai Chi Kok, Kowloon.	Valid		
No. 3156	23/02/04	22/02/09	Discharge of industrial trade effluent and all other wastewater arising from the works areas at North Portal of Route 9 – Eagle's Nest Tunnel and Associated Works (Contract HY/2003/02).	Valid		
Construction Noise	Permit (CN	P)	1			
GW-RN0185-07	11/5/07	10/11/07	Location: Tunnel North Portal site near Garden Villa Time Period: 0700-2300 (general holiday including Sundays) and 1900-2300 (any day not being a general holiday).	Expired		
GW-RN0230-07	06/06/07	05/12/07	Location: SHT-South Portal near Garden Villa Time Period: Any day between 2300-0700 on next day	Valid		
GW-RN0231-07	06/06/07	05/12/07	Location: SHT-North Portal near Tai Po Road and Keng Hau Road Time Period: Any day between 2300-0700 on next day	Valid		
GW-RN0252-07	18/06/07	17/12/07	Location: SHT-South Portal near Garden Villa Time Period: 0700-2300 (general holiday including Sundays) and 1900-2300 (any day not being a general holiday).	Valid		

Permit No.	Valid	Period	Details	Status
1 ci ilit ivo.	From	To	Details	Status
GW-RN0380-07	27/07/07	26/01/08	Location: Butterfly Valley, Lai Chi Kok Time Period: 0700-2300 (general holiday including Sundays) and 1900-2300 (any day not being a general holiday).	Valid
GW-RN0514-07	30/11/07	29/05/08	Location: SHT-North Portal near Tai Po Road and Keng Hau Road Time Period: 0700-2300 (general holiday including Sundays) and 1900-2300 (any day not being a general holiday).	Valid
GW-RN0515-07	30/11/07	29/05/08	Location: Tunnel North Portal Site near Garden Villa <i>Time Period</i> : 0700-2300 (general holiday including Sundays) and 1900-2300 (any day not being a general holiday).	Valid
GW-RN0513-07	30/11/07	29/05/08	Location: Tunnel South Portal Site at Butterfly Valley Time Period: 0700-2300 (general holiday including Sundays) and 1900-2300 (any day not being a general holiday).	Valid

- 4.6 Spot checks on truck overloading were also conducted during the site inspections since June 2006. No overloading incident was observed during the site inspections in the reporting month.
- 4.7 No non-conformance was identified during the site inspections in the reporting month. The observations and recommendations are summarized in **Table 4.2**.

 Table 4.2
 Observations and Recommendations of Site Audit for Civil Works

Parameters	Date	Observations / Recommendations Remedial Actions / R	
NIL			

4.8 The observations and recommendations arising from pervious month and followed up in the reporting month are summarized in **Table 4.3**.

Table 4.3 Observations and Recommendations of Site Audits Followed up for Pervious Month for Civil Works

Parameters	Date	Observations / Recommendations	Remedial Actions
Water Quality	31/10/07	Desilting channel bed was undergoes at Butterfly Valley. Runoff has been diverted to a catchpit at downstream. However the catchpit was observed without an adequate capacity so that the silty water has been discharging into the water course. The Contractor was advised to provide mitigation measure to settle runoff before discharging into the water course to stop the silty water running out from the site	Runoff has been observed settled before discharging during the site inspection on 7/11/07

Summary of Exceedances

1-hr and 24-hr TSP Monitoring

4.9 No Action/Limit Level exceedance for both 1-hour TSP and 24-hour TSP was recorded in the reporting month.

Construction noise

4.10 No Action/Limit Level exceedance for noise monitoring was recorded in the reporting month.

Implementation Status of Event Action Plans

4.11 The Event Action Plans for air quality and noise are presented in **Appendix J**.

Summary of Complaints and Prosecutions

- 4.12 No environmental related complaint or prosecution was received in the reporting month.
- 4.13 There were 22 environmental complaints and no prosecution received since the commencement of the Project. The updated Complaint Log is shown in **Appendix M**.

5. FUTURE KEY ISSUES

Key Issues for the Coming Month

- 5.1 Key issues to be considered in the coming months include:
 - Potential dust emission from slope works and road works.
 - Noise generation from road works.

Monitoring Schedule for the Next Month

5.2 The tentative environmental monitoring schedule for next month is shown in **Appendix C**.

Construction Program for the Next Month

5.3 The tentative construction program for civil works is provided in **Appendix L**. The major construction activities for civil works in the coming months include:

ENT Tunnel

• T&C for Tunnel ventilation lighting.

Butterfly Valley

• Haul road diversion, road works, step channel works, fill slope at SP-S2, u-channel, T&C on irrigation pipe & system and lighting for noise enclosure.

South Portal Building

• Metal meshing cladding, Cat Ladder for vent shaft, upper roof railing, plumbing & drainage (T&C), tunnel ventilation system (T&C), mechanical ventilation air condition and T&C.

North Portal Building

 Metal meshing cladding, cat ladder for vent shaft, upper roof railing, plumbing & drainage, tunnel ventilation system (T&C), mechanical ventilation air condition and T&C.

Toll Plaza's Structures and Administration Building

• Road works (including EVA Road & Loop Road No.2), Footbridge (metal cladding), roof tiles, metal curtain mesh cladding, mechanical ventilation air condition and T&C, false & external metal ceiling, plumbing and drainage (T&C), external hand rail installation, skirting and rubber & vinyl flooring, signage, carpet file, fire services and painting of wall.

Ventilation Building

• Cladding & hand rail installation, drainage works, fencing, mechanical ventilation air conditioning and T&C, plumbing & drainage, Tunnel Ventilation System and T&C.

SHT – South Portal Building

• Cat Ladder for vent shaft, mesh cladding, plumbing & drainage (T&C), upper roof railing, mechanical ventilation air conditioning and T&C, tunnel ventilation system (T&C).

SHT – North Portal Building

• Cat Ladder for vent shaft, mesh cladding, upper roof railing, plumbing & drainage, mechanical ventilation air conditioning and T&C, tunnel ventilation system (T&C).

SHT Tunnel & Remaining SHT/T3 Area

- Lighting testing, tunnel ventilation system (T&C) and fire services (T&C).
- 5.4 The tentative construction program for TCSS works is provided in **Appendix L**. The major site activities for TCSS works in the coming months include:
 - SAT for TCSS equipment at Tunnel, Butterfly Valley, Kiosk K3 & K4, South Portal Building, Toll Plaza, Administration Building and Ventilation Building.

6. CONCLUSIONS AND RECOMMENDATIONS

Conclusions

- 6.1 Environmental monitoring works were performed in the reporting month and all monitoring results were checked and reviewed.
- 6.2 No Action/Limit Level exceedance for 1-hour TSP and 24-hours TSP was recorded in the reporting month.
- 6.3 No Action/Limit Level exceedance for noise monitoring was recorded in the reporting month.
- 6.4 No environmental complaint or prosecution was received in the reporting month.

Recommendations

6.5 According to the environmental audit performed in the reporting month, the following recommendations were made:

Water Impact

- To closely monitor the capacity of existing de-silting facility on site, especially for the discharge at the site in Butterfly Valley.
- To keep the sedimentation facilities well maintained and perform de-silting regularly.
- To avoid accumulation of stagnant water on site.

Dust Impact

- To ensure that adequate water spray or other dust suppression measures are applied for slope cutting and the haul roads and stockpile on site.
- To cover idle soil slope surface and stockpile of dusty materials to prevent wind erosion.
- To ensure that all vehicles carrying dusty materials are properly covered before leaving the site.


Noise Impact


- To provide temporary noise barriers for noisy activities (such as breaking works).
- To reduce the number of noisy equipment in concurrent operation.

Waste/Chemical Management

- To ensure proper storage of chemical and chemical waste on site.
- To check for any accumulation of waste materials or rubbish on site.
- To avoid any discharge or accidental spillage of chemical waste or oil directly.

FIGURES

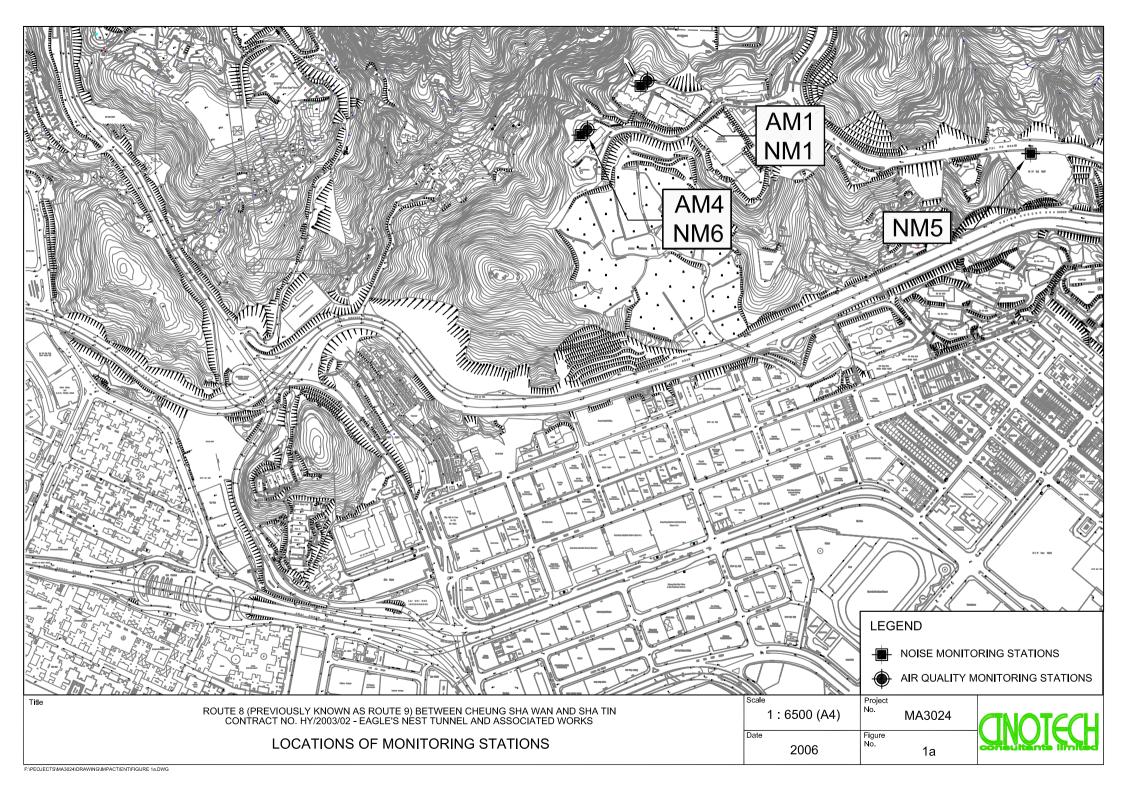

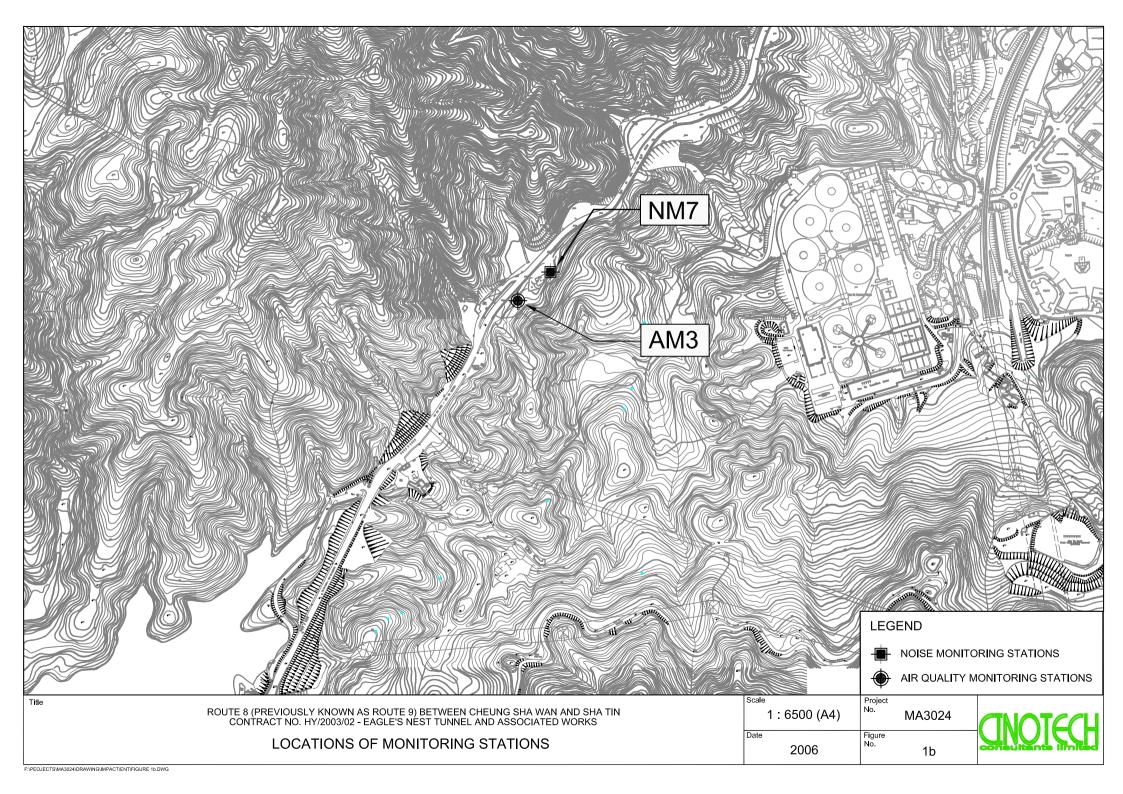

APPENDIX A ACTION AND LIMIT LEVELS

Appendix A - Action and Limit Levels (ENT)

1-Hour TSP

Location Action Level, μg/m ³		Limit Level, μg/m³
AM1	296	
AM3	350	500
AM4	294	

24-Hour TSP

Location	Action Level, μg/m ³	Limit Level, μg/m³
AM1	168	
AM3	200	260
AM4	170	

Construction Noise

Period	Action Level	Limit Level, dB(A)				
1 er iou	for all stations	NM1	NM5	NM6	NM7	
0700-1900 hrs on normal weekdays		70/65*	75	75	75	
0700-2300 hrs on holidays & 1900- 2300 hrs on all other days	When one documented complaint is received	-	70	65	60	
2300-0700 hrs of next day		-	55	50	45	

^(*) Since NM1 is an educational institution, the noise Limit Level (0700-1900 hrs on normal days) is taken as 70 dB(A). The Limit Level will be reduced to 65 dB(A) during school examination periods.

APPENDIX B COPIES OF CALIBRATION CERTIFCATES

High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET



File No. MA2027/A14/0025 Garden Vilia WK Station Operator: Date: 28-Sep-07 Next Due Date: 27-Nov-07 Equipment No.: A-01-14 Serial No. **Ambient Condition** Pressure, Pa (mmHg) Temperature, Ta (K) 301.3 761.6 Orifice Transfer Standard Information A-04-05 0.0575 0.0395 Slope, mc Intercept, bc Equipment No.: mc x Qstd + bc = $[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ Last Calibration Date: 12-Mar-07 Qstd = $\{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} -bc\} / mc$ Next Calibration Date: 11-Mar-08 Calibration of TSP Sampler Orfice HVS Calibration ΔH (orifice), Qstd (CFM) ΔW $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2} Y$ Point $[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ in. of water X - axis (HVS), in. of oil axis 1 12.2 3.48 59.79 7.7 2.76 2 10.4 2.52 3.21 55.15 6.4 3 7.6 2.74 47.04 5.0 2.23 5.1 2.25 38.41 1.84 3.3 1.81 30.77 1.44 By Linear Regression of Y on X Slope, mw = 0.04440.1048 Intercept, bw Correlation coefficient* = *If Correlation Coefficient < 0.990, check and recalibrate. Set Point Calculation From the TSP Field Calibration Curve, take Qstd = 43 CFM From the Regression Equation, the "Y" value according to mw x Qstd + bw = $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Therefore, Set Point; $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 4.09 Remarks: Signature: Date: Checked by:

High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA2027/A14/0026 Station Garden Vilia WK Operator: Date: 26-Nov-07 Next Due Date: 25-Jan-08 Equipment No.: A-01-14 Serial No. Ambient Condition Temperature, Ta (K) 294.7 Pressure, Pa (mmHg) 764.3 Orifice Transfer Standard Information A-04-05 Slope, mc 0.0575 Intercept, bc 0.0395 Equipment No.: mc x Qstd + bc = $[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ Last Calibration Date: 12-Mar-07 Qstd = $\{ [\Delta H \times (Pa/760) \times (298/Ta) \}^{1/2} -bc \} / mc$ Next Calibration Date: 11-Mar-08 Calibration of TSP Sampler Orfice HVS Calibration $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2} Y$ Qstd (CFM) ΔH (orifice), ΔW Point [\Delta H x (Pa/760) x (298/Ta)]1/2 in. of water (HVS), in. of oil X - axis axis 12.3 3.54 60.82 7.9 2.83 1 2 10.1 3.20 55.05 6.5 2.57 3 7.5 2.76 47.34 5.0 2.25 4 2.34 40.07 1.80 1.80 30.69 3.2 1.31 By Linear Regression of Y on X Slope, mw = 0.0507 Intercept, bw : ______-0.2181 Correlation coefficient* = 0.9977 *If Correlation Coefficient < 0.990, check and recalibrate. Set Point Calculation From the TSP Field Calibration Curve, take Qstd = 43 CFM From the Regression Equation, the "Y" value according to mw x Qstd + bw = $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Therefore, Set Point; $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 3.79 Remarks:

Date:

Date:

Conducted by: Wh. 1ang

Checked by: ()

Signature:

Signature:

High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA3024/17/0027 Station Government Quarter Operator: Next Due Date: 10-Nov-07 Date: 11-Sep-07 3460 Equipment No.: A-01-17 Serial No. **Ambient Condition** 300.3 Pressure, Pa (mmHg) 759.5 Temperature, Ta (K) Orifice Transfer Standard Information Equipment No.: A-04-05 Slope, mc 0.0575 Intercept, bc mc x Qstd + bc = $[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ Last Calibration Date: 12-Mar-07 Qstd = $\{ [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} -bc \} / mc$ Next Calibration Date: 11-Mar-08 Calibration of TSP Sampler Orfice HVS Calibration ΔH (orifice), Qstd (CFM) ΔW $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2} Y$ Point [ΔH x (Pa/760) x (298/Ta)]1/2 in. of water X - axis (HVS), in. of oil axis 1 10.5 3.23 55.43 7.5 2.73 2 8.6 2.92 50.10 6.0 2.44 6.2 2.48 42.44 4.3 2.07 3 4 2.11 1.75 4.5 36.05 3.1 1.81 30.77 1.44 5 3.3 2.1 By Linear Regression of Y on X Slope , mw = ______0.0513 Intercept, bw :______-0.1168 Correlation coefficient* = 0.9995 *If Correlation Coefficient < 0.990, check and recalibrate. **Set Point Calculation** From the TSP Field Calibration Curve, take Qstd = 43 CFM From the Regression Equation, the "Y" value according to mw x Qstd + bw = $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Therefore, Set Point; $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ Remarks:

High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET

CINOTECH

0	20 10 1000	77074		120	22724		MA3024/17/0028
Station	Government Qua	arter		DAGENA DELIVERAGE	:WK		
Date:	12-Nov-07				: <u>11-Jan</u>	Company of the Compan	
Equipment No.:	A-01-17	<u> </u>		Serial No.	. 3460	<u></u>	
		Special Control	Ambient	Condition	Mary 12 May 11 m		
Temperature, Ta (K) 293.6		293.6	Pressure, P	a (mmHg)		766.6	
			on the property	Proceedings of the Control of the Co			St
			ifice Transfer St			1 1000	
Equipme	Equipment No.: A-04-05		Slope, mc	0.0575	Intercep		0.0395
Last Calibr		12-Mar-07			$bc = [\Delta H \times (Pa/76)]$		
Next Calibr	ation Date:	11-Mar-08		$Qstd = \{ [\Delta H$	x (Pa/760) x (298	/Ta)] ^{1/2} -bc} /	me
			5. 100 MARCH 1967 - 3			nii neje	
- 36 C		The Transfers	P E + (10) (11-50) - CAL CO	f TSP Sampler	1944 - 1944 - 1944 - 1944 - 1944 - 1944 - 1944 - 1944 - 1944 - 1944 - 1944 - 1944 - 1944 - 1944 - 1944 - 1944	t. Two	And I
Calibration	ATT (= 1C - 1	Orf	D. Santa	O-44 (OP) 6		HVS	(a) (a) (b) (a) (b) (a) (b) (b) (c) (c) (c) (c) (c) (c) (c) (c) (c) (c
Point	ΔH (orifice), in. of water	[ΔH x (Pa/760)) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of oil	[ΔW x (Pa/76	50) x (298/Ta)] ^{1/2} Y- axis
1	11.0	3.36		57.68	7.7	# 52 S W	2.81
2	8.6	2.97		50.92	6.3		2.54
3	6.3	2.54		43.48	4.4		2.12
4	5.0	2	.26	38.66	3.2		1.81
5	3.2	_ 1.	.81	30.79	1.8		1.36
Correlation c	0.0549 oefficient* = Coefficient < 0.990	0.99	71	Intercept, bw	-0.304	4	<i>a</i>
		A Maria	Set Point (alculation	47 - AZ		
From the TSP Fi	eld Calibration Co	rve, take Ostd =		3110311111031	and the second second	300	
	sion Equation, the						
	1		DE 177.1 - 19-19-75 C.		5227		ï
		mw x Q	$std + bw = [\Delta W]$	x (Pa/760) x (2	98/Ta)] ^{1/2}		
Therefore, Se	et Point; W = (my	$v \times Qstd + bw)^2$	x (760/Pa)x(Γa / 298) =	4.13		
		* 1	17 -				
Remarks:		11 To 12 To 12 XX					· · ·
	711	Signature:	Ikwai		M .	Date: _	12 NOV 07
Checked by:	1+	Signature:	YL_			Date:	12 Warson I

WELLAB LTD.

Unit C, 1/F, Goldlion Holdings Center 13-15 Yuen Shun Circuit, Shatin, Hong Kong.

Tel: (852) 2898 7388 Fax: (852) 2898 7076

TEST REPORT

APPLICANT: Cinotech Consultants Limited

1602-1610 Delta House,

3 On Yiu Street, Shatin, N.T. Test Report No.: C/07/70502
Date of Issue: 2007-05-02
Date Received: 2007-05-01
Date Tested: 2007-05-01
Date Completed: 2007-05-02

ATTN:

Mr. Henry Leung

Page:

1 of 1

Certificate of Calibration

Item for calibration:

Description

: RS232 Integral Vane Digital Anemometer

Manufacturer

: AZ Instrument

Model No.

: 451104

Serial No.

: 9020746

Equipment No.

: A-03-01

Test conditions:

Room Temperature

: 21 degree Celsius

Relative Humidity

: 65%

Pressure

: 101.3 kPa

Methodology:

The anemometer has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Results	Reference Set Point	Instrument Readings
Measuring Air Velocity, m/s	2.00	2.00
Temperature, °C	21.0	21.0

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE

Senior Chemist



TISCH ENVIROMENTAL, INC.
145 SOUTH MIAMI AVE.
VILLAGE OF CLEVES, OH 45002
513.467.9000
877.263.7610 TOLL FREE
513.467.9009 FAX
WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Ma Operator	Ta (K) - Pa (mm) -	294 74676				
PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1 2 3 4 5	NA NA NA NA	NA NA NA NA	1.00 1.00 1.00 1.00	1.3890 0.9850 0.8810 0.8410 0.6950	3.2 6.3 7.8 8.6 12.5	2.00 4.00 5.00 5.50 8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)		Va .	(x axis) Qa	(y axis)
0.9917 0.9876 0.9854 0.9844 0.9792	0.7139 1.0026 1.1185 1.1706 1.4090	1.4113 1.9959 2.2315 2.3405 2.8227		0.9957 0.9916 0.9894 0.9884 0.9832	0.7168 1.0067 1.1231 1.1753 1.4147	0.8874 1.2549 1.4030 1.4715 1.7747
Qstd slor intercept coefficie	(b) = ent (r) =	2.03154 -0.03970 0.99999		Qa slope intercept coefficie	(b) = ent (r) =	1.27212 -0.02496 0.99999
y axis =	SQRT [H20 (Pa/760)(298/	ra)]	y axis =	SQRT[H2O(T	'a/Pa)]

CALCULATIONS

Vstd = Diff. Vol[(Pa-Diff. Hg)/760](298/Ta)
Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]
Qa = Va/Time


For subsequent flow rate calculations:

Qstd = $1/m\{[SQRT(H2O(Pa/760)(298/Ta))] - b\}$ Qa = $1/m\{[SQRT H2O(Ta/Pa)] - b\}$



TISCH ENVIROMENTAL, INC. 145 SOUTH MIAMI AVE. VILLAGE OF CLEVES, OH 45002 513.467.9000 877.263.7610 TOLL FREE 513.467.9009 FAX WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

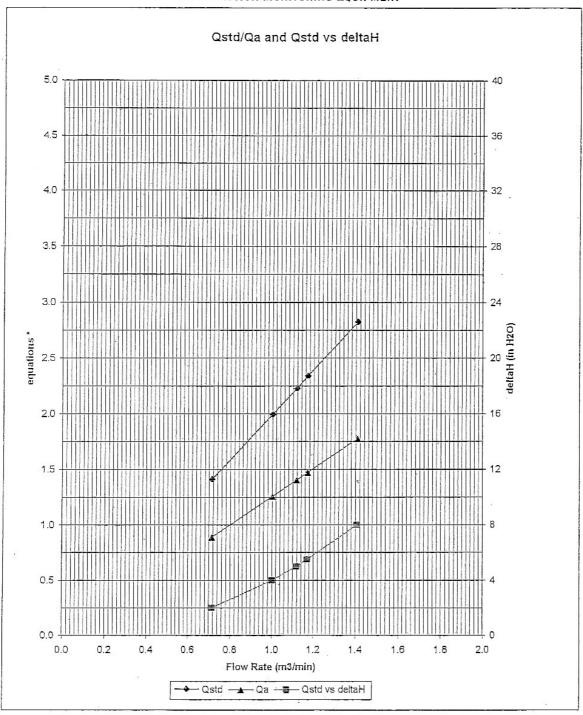

* y-axis equations:

Qstd series:

$$\sqrt{\Delta \ H \left(\frac{P \ a}{P \ s \ t \ d}\right) \left(\frac{T \ s \ t \ d}{T \ a}\right)}$$

Qa series:

$$\sqrt{(\Delta H (Ta/Pa))}$$

WELLAB LTD.

Unit C, 1/F, Goldlion Holdings Center 13-15 Yuen Shun Circuit, Shatin, Hong Kong.

Tel: (852) 2898 7388 Fax: (852) 2898 7076

TEST REPORT

APPLICANT: Cinotech Consultants Limited

1602-1610 Delta House,

3 On Yiu Street, Shatin, N.T. Test Report No.: C/N/61215/1
Date of Issue: 2006-12-15
Date Received: 2006-12-14
Date Tested: 2006-12-15
Date Completed: 2006-12-15
Next Due Date: 2007-12-14

ATTN: Mr. Henry Leung Page: 1 of 1

Certificate of Calibration

Item for calibration:

Description : Integrating Sound Level Meter

Manufacturer : Brüel & Kjær Model No. : B&K 2238 Serial No. : 2337665 Microphone No. : 2289749 Equipment No. : N-01-01

Test conditions:

Room Temperatre : 20 degree Celsius

Relative Humidity : 60%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB	
94	94.0	
114	114.0	

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE
Operation Manager

This test document cannot be reproduced in any way, except in full context, without the prior approval in writing of the laboratory.

WELLAB LTD.

Unit C, 1/F, Goldlion Holdings Center 13-15 Yuen Shun Circuit, Shatin, Hong Kong.

Tel: (852) 2898 7388 Fax: (852) 2898 7076

TEST REPORT

APPLICANT: Cinotech Consultants Limited

1602-1610 Delta House,

3 On Yiu Street, Shatin, N.T.

 Test Report No.:
 C/N/61116/1

 Date of Issue:
 2006-11-16

 Date Received:
 2006-11-15

 Date Tested:
 2006-11-15

 Date Completed:
 2006-11-16

 Next Due Date:
 2007-11-15

ATTN:

Mr. Henry Leung

Page:

1 of 1

Certificate of Calibration

Item for calibration:

Description ·

: Integrating Sound Level Meter

Manufacturer Model No.

: Brüel & Kjær : B&K 2238

Serial No.

: 2337666 : 2289750

Microphone No. Equipment No.

: N-01-02

Test conditions:

Room Temperatre

: 20 degree Celsius

Relative Humidity

: 59%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB	
94	94.0	
114	114.0	

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE

Operation Manager



Unit C, 1/F., Goldlion Holdings Center, 13-15 Yuen Shun Circuit, Shatin, NT, HK. Tel: 2898 7388 Fax: 2898 7076 Website: www.wellab.com.hk

TEST REPORT

APPLICANT: Cinotech Consultants Limited

Room 1710, Technology Park,

18 On Lai Street,

Shatin, NT, Hong Kong

Test Report No.: C/N/71116/1
Date of Issue: 2007-11-16
Date Received: 2007-11-15
Date Tested: 2007-11-15
Date Completed: 2007-11-16
Next Due Date: 2008-11-15

ATTN:

Mr. Henry Leung

Page:

1 of 1

Certificate of Calibration

Item for calibration:

Description

: Integrating Sound Level Meter

Manufacturer Model No. : Brüel & Kjær : B&K 2238

Serial No.

: 2337666

Microphone No. Equipment No.

: 2289750 : N-01-02

Test conditions:

Room Temperatre

: 20 degree Celsius

Relative Humidity

: 59%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB	
94	94.0	
114	114.0	

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE Senior Chemist

This report may not be reproduced except with prior written approval from WELLAB LIMITED and the results relate only to the items calibrated or tested.





APPLICANT: Cinotech Consultants Limited

1601-1610 Delta House,

3 On Yiu Street, Shatin, N.T. Test Report No.: C/N/70903-1
Date of Issue: 2007-09-03
Date Received: 2007-09-01
Date Tested: 2007-09-03
Date Completed: 2007-09-03
Next Due Date: 2008-09-02

ATTN:

Mr. Henry Leung

Page:

1 of 1

Certificate of Calibration

Item for calibration:

Description

: Integrating Sound Level Meter

Manufacturer Model No.

: Brüel & Kjær : B&K 2238

Serial No.
Microphone No.

: 2359311 : 2346382

Equipment No.

: N-01-03

Test conditions:

Room Temperatre

: 22 degree Celsius

Relative Humidity

: 62%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB	
94	94.0	
114	114.0	

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE

Senior Chemist





APPLICANT: Cinotech Consultants Limited

1602-1610 Delta House,

3 On Yiu Street, Shatin, N.T. Test Report No.: C/N/70903-2
Date of Issue: 2007-09-03
Date Received: 2007-09-01
Date Tested: 2007-09-03
Date Completed: 2007-09-03
Next Due Date: 2008-09-02

ATTN:

Mr. Henry Leung

Page:

1 of 1

Certificate of Calibration

Item for calibration:

Description : Integrating Sound Level Meter

Manufacturer : Brüel & Kjær Model No. : B&K 2238 Serial No. : 2359303 Equipment No. : N-01-04

Test conditions:

Room Temperatre : 22 degree Celsius

Relative Humidity : 62%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB	
94	94.0	
114	114.0	

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE

Senior Chemist





APPLICANT: Cinotech Consultants Limited

Room 1710, Technology Park,

18 On Lai Street,

Shatin, NT, Hong Kong

Test Report No.: C/N/71015/1
Date of Issue: 2007-10-15
Date Received: 2007-10-13
Date Tested: 2007-10-13
Date Completed: 2007-10-15
Next Due Date: 2008-10-14

ATTN:

Mr. Henry Leung

Page:

1 of 1

Certificate of Calibration

Item for calibration:

Description

: Integrating Sound Level Meter

Manufacturer

: Brüel & Kjær

Model No.

: B&K 2238

Serial No. Microphone No. : 2394976 : 2407349

Equipment No.

: N-01-05

Test conditions:

Room Temperatre

: 21 degree Celsius

Relative Humidity

: 60%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB	
94	94.0	
114	114.0	

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE

Senior Chemist

This report may not be reproduced except with prior written approval from WELLAB LIMITED and the results relate only to the items calibrated or tested.

WELLAB LTD.

Unit C, 1/F, Goldlion Holdings Center 13-15 Yuen Shun Circuit, Shatin, Hong Kong.

Tel: (852) 2898 7388 Fax: (852) 2898 7076

TEST REPORT

APPLICANT: Cinotech Consultants Limited

1602-1610 Delta House,

3 On Yiu Street, Shatin, N.T.

 Test Report No.:
 C/N/61116/2

 Date of Issue:
 2006-11-16

 Date Received:
 2006-11-15

 Date Tested:
 2006-11-15

 Date Completed:
 2006-11-16

 Next Due Date:
 2007-11-15

ATTN:

Mr. Henry Leung

Page:

1 of 1

Item for calibration:

Description

: Acoustical Calibrator

Manufacturer

: Brüel & Kjær

Model No.

: 4231

Serial No.

: 2326353

Project No.

: C13

Equipment No.

: N-02-01

Test conditions:

Room Temperatre

: 20 degree Celsius

Relative Humidity

: 59%

Pressure

: 1015.2 hPa

Methodology:

The sound calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level	Measured SPL	Tolerance
At 94 dB SPL	94.0	$94.0 \pm 0.1~\mathrm{dB}$

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE

Operation Manager



APPLICANT: Cinotech Consultants Limited

Room 1710, Technology Park,

18 On Lai Street,

Shatin, NT, Hong Kong

Test Report No.:	C/N/71116/2	
Date of Issue:	2007-11-16	
Date Received:	2007-11-15	
Date Tested:	2007-11-15	
Date Completed:	2007-11-16	
Next Due Date:	2008-11-15	

ATTN:

Mr. Henry Leung

Page:

1 of 1

Item for calibration:

Description

: Acoustical Calibrator

Manufacturer

: Brüel & Kjær

Model No. Serial No. : 4231 : 2326353

Project No.

: C13

Equipment No.

: N-02-01

Test conditions:

Room Temperatre

: 20 degree Celsius

Relative Humidity

: 59%

Pressure

: 1015.2 hPa

Methodology:

The sound calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE Senior Chemist

This report may not be reproduced except with prior written approval from WELLAB LIMITED and the results relate only to the items calibrated or tested.

WELLAB LTD.

Unit C, 1/F, Goldlion Holdings Center 13-15 Yuen Shun Circuit, Shatin, Hong Kong.

Tel: (852) 2898 7388 Fax: (852) 2898 7076

TEST REPORT

APPLICANT: Cinotech Consultants Limited

1602-1610 Delta House,

3 On Yiu Street, Shatin, N.T.

Test Report No.:	C/06/70305
Date of Issue:	2007-03-05
Date Received:	2007-03-03
Date Tested:	2007-03-03
Date Completed:	2007-03-05
Next Due Date:	2008-03-04

ATTN:

Mr. Henry Leung

Page:

1 of 1

Item for calibration:

Description

: Acoustical Calibrator

Manufacturer

: Brüel & Kjær

Model No. Serial No.

: 4231 : 2343007

Project No.

: C13

Equipment No.

: N-02-02

Test conditions:

Room Temperatre

: 20 degree Celsius

Relative Humidity

: 65%

Pressure

: 1020.1hPa

Methodology:

The sound calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.2 dB

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE

Operation Manager

This test document cannot be reproduced in any way, except in full context, without the prior approval in writing of the laboratory.



Unit C, 1/F., Goldlion Holdings Center, 13-15 Yuen Shun Circuit, Shatin, NT, HK. Tel: 2898 7388 Fax: 2898 7076 Website: www.wellab.com.hk

TEST REPORT

APPLICANT: Cinotech Consultants Limited

1602-1610 Delta House,

3 On Yiu Street, Shatin, N.T. Test Report No.: C/N/70903-3
Date of Issue: 2007-09-03
Date Received: 2007-09-01
Date Tested: 2007-09-03
Date Completed: 2007-09-03
Next Due Date: 2008-09-02

ATTN:

Mr. Henry Leung

Page:

1 of 1

Item for calibration:

Description

: Acoustical Calibrator

Manufacturer

: Brüel & Kjær

Model No.

: 4231

Serial No.

: 2412367

Equipment No.

: N-02-03

Test conditions:

Room Temperatre

: 22 degree Celsius

Relative Humidity

: 62%

Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.

PATRICK TSE

Senior Chemist

APPENDIX C ENVIRONMENTAL MONITORING AND AUDIT SCHEDULE

Environmental Monitoring for Eagle's Nest Tunnel Tentative Air Quality and Noise Monitoring Schedule for November 2007

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
28-Oct	29-Oct	30-Oct	31-Oct	1-Nov	2-Nov	3-Nov
	24 hr TSP	1 hr TSP	1 hr TSP	1 hr TSP Noise		24 hr TSP
4-Nov	5-Nov	6-Nov	7-Nov	8-Nov	9-Nov	10-Nov
	1 hr TSP	1 hr TSP		1 hr TSP Noise	24 hr TSP	
11-Nov	12-Nov	13-Nov	14-Nov	15-Nov	16-Nov	17-Nov
	1 hr TSP	1 hr TSP		24 hr TSP	1 hr TSP Noise	
18-Nov	19-Nov	20-Nov	21-Nov	22-Nov	23-Nov	24-Nov
	1 hr TSP	1 hr TSP	24 hr TSP	1 hr TSP Noise		
25-Nov	26-Nov	27-Nov	28-Nov	29-Nov	30-Nov	1-Dec
	1 hr TSP	24 hr TSP	1 hr TSP	1 hr TSP Noise		

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

AM3 Garden Villa AM4 Government Quarters NM6 Government Quarters NM7 Garden Villa Carlton

NM6 Government Quarters NM7 Garden Villa

Environmental Monitoring for Eagle's Nest Tunnel Tentative Air Quality and Noise Monitoring Schedule for December 2007

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
2-Dec	3-Dec	4-Dec	5-Dec	6-Dec	7-Dec	8-Dec
	24 hr TSP	1 hr TSP		1 hr TSP Noise	1 hr TSP	24 hr TSP
9-Dec	10-Dec	11-Dec	12-Dec	13-Dec	14-Dec	15-Dec
	1 hr TSP	1 hr TSP		1 hr TSP Noise	24 hr TSP	
16-Dec	17-Dec	18-Dec	19-Dec	20-Dec	21-Dec	22-Dec
	1 hr TSP	1 hr TSP	24 hr TSP	1 hr TSP Noise		
23-Dec	24-Dec	25-Dec	26-Dec	27-Dec	28-Dec	29-Dec
	1 hr TSP		24 hr TSP	1 hr TSP	1 hr TSP Noise	
30-Dec	31-Dec	1-Jan	2-Jan	3-Jan	4-Jan	5-Jan
		1 hr TSP 24 hr TSP	1 hr TSP	1 hr TSP Noise		

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

AM3 Garden Villa AM4 Government Quarters NM6 Government Quarters NM7 Garden Villa Carlton

NM6 Government Quarters NM7 Garden Villa

APPENDIX D WIND DATA

Date	Time	Wind Speed m/s	Direction
1-Nov-2007	0:00	5.0	W
1-Nov-2007	1:00	4.0	WNW
1-Nov-2007	2:00	5.0	WNW
1-Nov-2007	3:00	5.0	WSW
1-Nov-2007	4:00	7.0	WNW
1-Nov-2007	5:00	9.0	W
1-Nov-2007	6:00	5.0	W
1-Nov-2007	7:00	8.0	WNW
1-Nov-2007	8:00	9.0	W
1-Nov-2007	9:00	7.0	WNW
1-Nov-2007	10:00	6.0	WNW
1-Nov-2007	11:00	3.0	WNW
1-Nov-2007	12:00	3.0	WSW
1-Nov-2007	13:00	5.0	WSW
1-Nov-2007	14:00	6.0	WSW
1-Nov-2007	15:00	6.0	WSW
1-Nov-2007	16:00	7.0	WSW
1-Nov-2007	17:00	8.0	WSW
1-Nov-2007	18:00	7.0	WSW
1-Nov-2007	19:00	6.0	W
1-Nov-2007	20:00	9.0	WSW
1-Nov-2007	21:00	10.0	WSW
1-Nov-2007	22:00	9.0	WSW
1-Nov-2007	23:00	8.0	WSW
2-Nov-2007	0:00	6.0	WSW
2-Nov-2007	1:00	6.0	WSW
2-Nov-2007	2:00	8.0	WSW
2-Nov-2007	3:00	6.0	WSW
2-Nov-2007	4:00	2.0	SW
2-Nov-2007	5:00	2.0	WNW
2-Nov-2007	6:00	5.0	W
2-Nov-2007	7:00	5.0	WSW
2-Nov-2007	8:00	5.0	WNW
2-Nov-2007	9:00	5.0	WNW
2-Nov-2007	10:00	10.0	WNW
2-Nov-2007	11:00	9.0	WNW
2-Nov-2007	12:00	7.0	WNW
2-Nov-2007	13:00	5.0	W
2-Nov-2007	14:00	3.0	SSW
2-Nov-2007	15:00	4.0	WSW
2-Nov-2007 2-Nov-2007	16:00	2.0	WSW
2-Nov-2007 2-Nov-2007	17:00	1.0	SW
2-Nov-2007 2-Nov-2007	18:00	2.0	SW
2-Nov-2007 2-Nov-2007	19:00	5.0	SW
2-Nov-2007 2-Nov-2007	20:00	5.0	SW
2-Nov-2007 2-Nov-2007	21:00	2.0	SW
2-Nov-2007 2-Nov-2007	22:00	4.0	SW
2-Nov-2007 2-Nov-2007	23:00	5.0	SW
3-Nov-2007	0:00	6.0	WSW
3-Nov-2007 3-Nov-2007	1:00	4.0	WSW
	2:00	2.0	SW
3-Nov-2007 3-Nov-2007			
.>-INUV-ZUU/	3:00	2.0	SW
3-Nov-2007	4:00	1.0	SW

Date	Time	Wind Speed m/s	Direction
3-Nov-2007	6:00	1.0	WNW
3-Nov-2007	7:00	4.0	WNW
3-Nov-2007	8:00	5.0	W
3-Nov-2007	9:00	8.0	WNW
3-Nov-2007	10:00	9.0	W
3-Nov-2007	11:00	8.0	WNW
3-Nov-2007	12:00	6.0	WNW
3-Nov-2007	13:00	6.0	W
3-Nov-2007	14:00	6.0	SW
3-Nov-2007	15:00	5.0	WSW
3-Nov-2007	16:00	3.0	WSW
3-Nov-2007	17:00	2.0	SSW
3-Nov-2007	18:00	0.0	SSW
3-Nov-2007	19:00	0.0	
3-Nov-2007	20:00	0.0	
3-Nov-2007	21:00	0.0	
3-Nov-2007	22:00	0.0	
3-Nov-2007	23:00	0.0	
4-Nov-2007	0:00	0.0	
4-Nov-2007	1:00	0.0	
4-Nov-2007	2:00	0.0	SSW
4-Nov-2007	3:00	3.0	SW
4-Nov-2007	4:00	3.0	SW
4-Nov-2007	5:00	1.0	SW
4-Nov-2007	6:00	3.0	SW
4-Nov-2007	7:00	7.0	WSW
4-Nov-2007	8:00	9.0	WSW
4-Nov-2007	9:00	10.0	WSW
4-Nov-2007	10:00	10.0	WNW
4-Nov-2007	11:00	8.0	WNW
4-Nov-2007	12:00	8.0	WSW
4-Nov-2007	13:00	7.0	SW
4-Nov-2007	14:00	4.0	SW
4-Nov-2007	15:00	5.0	WSW
4-Nov-2007	16:00	3.0	SSW
4-Nov-2007	17:00	3.0	W
4-Nov-2007	18:00	1.0	W
4-Nov-2007	19:00	0.0	SSW
4-Nov-2007	20:00	0.0	
4-Nov-2007	21:00	0.0	
4-Nov-2007 4-Nov-2007	22:00	0.0	
4-Nov-2007 4-Nov-2007	23:00	0.0	
5-Nov-2007	0:00	0.0	
			 SS/M
5-Nov-2007	1:00 2:00	0.0	SSW SSW
5-Nov-2007	3:00		SSW
5-Nov-2007 5-Nov-2007		1.0	SW
	4:00	1.0	
5-Nov-2007	5:00	2.0	SW
5-Nov-2007	6:00	3.0	SW
5-Nov-2007	7:00	2.0	SW
5-Nov-2007	8:00	2.0	SW
5-Nov-2007	9:00	7.0	WNW
5-Nov-2007	10:00	8.0	WNW

Date	Time	Wind Speed m/s	Direction
5-Nov-2007	12:00	8.0	WNW
5-Nov-2007	13:00	6.0	WSW
5-Nov-2007	14:00	4.0	WSW
5-Nov-2007	15:00	5.0	W
5-Nov-2007	16:00	7.0	W
5-Nov-2007	17:00	6.0	SW
5-Nov-2007	18:00	4.0	SW
5-Nov-2007	19:00	3.0	SW
5-Nov-2007	20:00	4.0	SW
5-Nov-2007	21:00	4.0	SW
5-Nov-2007	22:00	6.0	WSW
5-Nov-2007	23:00	8.0	WSW
6-Nov-2007	0:00	7.0	SW
6-Nov-2007	1:00	8.0	WSW
6-Nov-2007	2:00	7.0	SW
6-Nov-2007	3:00	3.0	SW
6-Nov-2007	4:00	5.0	SW
6-Nov-2007	5:00	7.0	WSW
6-Nov-2007	6:00	6.0	WSW
6-Nov-2007	7:00	1.0	WNW
6-Nov-2007	8:00	1.0	WSW
6-Nov-2007	9:00	5.0	WSW
6-Nov-2007	10:00	4.0	WNW
6-Nov-2007	11:00	5.0	WNW
6-Nov-2007	12:00	4.0	WNW
6-Nov-2007	13:00	5.0	SW
6-Nov-2007	14:00	4.0	W
6-Nov-2007	15:00	10.0	WNW
6-Nov-2007	16:00	8.0	W
6-Nov-2007	17:00	6.0	SW
6-Nov-2007	18:00	3.0	SW
6-Nov-2007	19:00	4.0	SW
6-Nov-2007	20:00	7.0	WSW
6-Nov-2007	21:00	7.0	WSW
6-Nov-2007	22:00	7.0	SW
6-Nov-2007	23:00	10.0	SW
			WSW
7-Nov-2007	0:00	9.0	
7-Nov-2007	1:00	8.0	SW
7-Nov-2007	2:00	7.0	WSW WSW
7-Nov-2007	3:00	8.0	_
7-Nov-2007	4:00	7.0	WSW
7-Nov-2007	5:00	7.0	SW
7-Nov-2007	6:00	8.0	WSW
7-Nov-2007	7:00	6.0	WSW
7-Nov-2007	8:00	7.0	WSW
7-Nov-2007	9:00	8.0	WSW
7-Nov-2007	10:00	9.0	W
7-Nov-2007	11:00	11.0	WNW
7-Nov-2007	12:00	8.0	WNW
7-Nov-2007	13:00	7.0	W
7-Nov-2007	14:00	7.0	WNW
7-Nov-2007	15:00	8.0	W
7-Nov-2007	16:00	6.0	W
7-Nov-2007	17:00	6.0	SW

Date	Time	Wind Speed m/s	Direction
7-Nov-2007	18:00	6.0	WSW
7-Nov-2007	19:00	4.0	SW
7-Nov-2007	20:00	7.0	SW
7-Nov-2007	21:00	8.0	WSW
7-Nov-2007	22:00	7.0	SW
7-Nov-2007	23:00	6.0	WSW
8-Nov-2007	0:00	6.0	SW
8-Nov-2007	1:00	2.0	SW
8-Nov-2007	2:00	2.0	W
8-Nov-2007	3:00	5.0	WSW
8-Nov-2007	4:00	7.0	WSW
8-Nov-2007	5:00	7.0	WSW
8-Nov-2007	6:00	10.0	WNW
8-Nov-2007	7:00	6.0	W
8-Nov-2007	8:00	7.0	W
8-Nov-2007	9:00	8.0	WNW
8-Nov-2007	10:00	7.0	W
8-Nov-2007	11:00	8.0	W
8-Nov-2007	12:00	10.0	W
8-Nov-2007	13:00	7.0	W
8-Nov-2007	14:00	6.0	W
8-Nov-2007	15:00	6.0	WSW
8-Nov-2007	16:00	7.0	WSW
8-Nov-2007	17:00	6.0	WSW
8-Nov-2007	18:00	6.0	WSW
8-Nov-2007	19:00	6.0	SW
8-Nov-2007	20:00	9.0	SW
8-Nov-2007	21:00	9.0	WNW
8-Nov-2007	22:00	8.0	W
8-Nov-2007	23:00	6.0	SW
9-Nov-2007	0:00	6.0	WSW
9-Nov-2007	1:00	5.0	WSW
9-Nov-2007	2:00	4.0	W
9-Nov-2007	3:00	6.0	WNW
9-Nov-2007	4:00	6.0	W
9-Nov-2007	5:00	4.0	WNW
9-Nov-2007	6:00	0.0	W
9-Nov-2007	7:00	2.0	WNW
9-Nov-2007	8:00	2.0	W
9-Nov-2007	9:00	7.0	WNW
9-Nov-2007	10:00	12.0	W
9-Nov-2007	11:00	11.0	WNW
9-Nov-2007	12:00	9.0	W
9-Nov-2007	13:00	8.0	W
9-Nov-2007	14:00	8.0	WNW
9-Nov-2007	15:00	6.0	W
9-Nov-2007	16:00	5.0	W
9-Nov-2007	17:00	2.0	SSW
9-Nov-2007	18:00	0.0	SSW
9-Nov-2007 9-Nov-2007	19:00	0.0	
9-Nov-2007	20:00	0.0	SSW
9-Nov-2007 9-Nov-2007	21:00	2.0	WNW
	22:00		WSW
9-Nov-2007		1.0	1/// 2.1//

Date	Time	Wind Speed m/s	Direction
10-Nov-2007	0:00	2.0	WSW
10-Nov-2007	1:00	1.0	WSW
10-Nov-2007	2:00	4.0	SW
10-Nov-2007	3:00	3.0	SW
10-Nov-2007	4:00	1.0	SW
10-Nov-2007	5:00	0.0	SSW
10-Nov-2007	6:00	0.0	
10-Nov-2007	7:00	0.0	
10-Nov-2007	8:00	0.0	
10-Nov-2007	9:00	3.0	WNW
10-Nov-2007	10:00	9.0	WNW
10-Nov-2007	11:00	7.0	W
10-Nov-2007	12:00	7.0	SW
10-Nov-2007	13:00	6.0	WNW
10-Nov-2007	14:00	6.0	WNW
10-Nov-2007	15:00	5.0	WNW
10-Nov-2007	16:00	5.0	W
10-Nov-2007	17:00	5.0	WSW
10-Nov-2007	18:00	6.0	W
10-Nov-2007	19:00	5.0	W
10-Nov-2007	20:00	0.0	WNW
10-Nov-2007	21:00	0.0	W
10-Nov-2007	22:00	0.0	WSW
10-Nov-2007	23:00	1.0	W
11-Nov-2007	0:00	5.0	W
11-Nov-2007	1:00	5.0	SW
11-Nov-2007	2:00	6.0	W
11-Nov-2007	3:00	4.0	WSW
11-Nov-2007	4:00	4.0	SW
11-Nov-2007	5:00	4.0	SW
11-Nov-2007	6:00	4.0	SW
11-Nov-2007	7:00	1.0	SW
11-Nov-2007	8:00	1.0	WNW
11-Nov-2007	9:00	6.0	WNW
11-Nov-2007	10:00	5.0	SW
11-Nov-2007	11:00	5.0	WNW
11-Nov-2007	12:00	4.0	WSW
11-Nov-2007	13:00	5.0	WNW
11-Nov-2007	14:00	6.0	WNW
11-Nov-2007	15:00	5.0	WNW
11-Nov-2007	16:00	6.0	W
11-Nov-2007	17:00	6.0	WNW
11-Nov-2007	18:00	5.0	WSW
11-Nov-2007	19:00	6.0	WSW
11-Nov-2007	20:00	7.0	WNW
11-Nov-2007 11-Nov-2007	21:00	7.0	WNW
11-Nov-2007	22:00	6.0	WNW
11-Nov-2007	23:00	7.0	WNW
12-Nov-2007	0:00	7.0	WNW
12-Nov-2007 12-Nov-2007	1:00	7.0	WNW
	2:00	7.0	W
12-Nov-2007			W
12-Nov-2007	3:00	6.0	
12-Nov-2007	4:00	5.0	WSW
12-Nov-2007	5:00	4.0	SW

Date	Time	Wind Speed m/s	Direction
12-Nov-2007	6:00	5.0	SW
12-Nov-2007	7:00	5.0	SW
12-Nov-2007	8:00	6.0	SW
12-Nov-2007	9:00	7.0	W
12-Nov-2007	10:00	7.0	W
12-Nov-2007	11:00	8.0	W
12-Nov-2007	12:00	8.0	WNW
12-Nov-2007	13:00	7.0	WNW
12-Nov-2007	14:00	6.0	NNW
12-Nov-2007	15:00	9.0	WNW
12-Nov-2007	16:00	7.0	WNW
12-Nov-2007	17:00	6.0	WNW
12-Nov-2007	18:00	5.0	W
12-Nov-2007 12-Nov-2007	19:00	6.0	W
12-Nov-2007	20:00	6.0	W
			W
12-Nov-2007	21:00	4.0	WSW
12-Nov-2007	22:00	6.0	WNW
12-Nov-2007	23:00	7.0	
13-Nov-2007	0:00	8.0	W
13-Nov-2007	1:00	7.0	WNW
13-Nov-2007	2:00	4.0	W
13-Nov-2007	3:00	6.0	WSW
13-Nov-2007	4:00	7.0	WSW
13-Nov-2007	5:00	7.0	SW
13-Nov-2007	6:00	5.0	SW
13-Nov-2007	7:00	4.0	SSW
13-Nov-2007	8:00	3.0	SW
13-Nov-2007	9:00	5.0	W
13-Nov-2007	10:00	8.0	W
13-Nov-2007	11:00	9.0	WNW
13-Nov-2007	12:00	9.0	W
13-Nov-2007	13:00	8.0	WNW
13-Nov-2007	14:00	5.0	WSW
13-Nov-2007	15:00	6.0	WNW
13-Nov-2007	16:00	4.0	W
13-Nov-2007	17:00	2.0	WNW
13-Nov-2007	18:00	1.0	WSW
13-Nov-2007	19:00	0.0	WSW
13-Nov-2007	20:00	0.0	WSW
13-Nov-2007	21:00	0.0	WSW
13-Nov-2007	22:00	0.0	
13-Nov-2007	23:00	1.0	SW
14-Nov-2007	0:00	2.0	SW
14-Nov-2007	1:00	5.0	W
14-Nov-2007	2:00	5.0	WSW
14-Nov-2007	3:00	5.0	SW
14-Nov-2007	4:00	5.0	SW
14-Nov-2007	5:00	5.0	WSW
14-Nov-2007	6:00	5.0	SW
14-Nov-2007	7:00	3.0	SW
14-Nov-2007	8:00	3.0	SW
	0.00	0.0	577
	Q·00	8 0	\\/\\\\
14-Nov-2007 14-Nov-2007	9:00 10:00	8.0 8.0	WNW WNW

Date	Time	Wind Speed m/s	Direction
14-Nov-2007	12:00	6.0	W
14-Nov-2007	13:00	6.0	WNW
14-Nov-2007	14:00	5.0	WSW
14-Nov-2007	15:00	5.0	WNW
14-Nov-2007	16:00	4.0	WSW
14-Nov-2007	17:00	5.0	W
14-Nov-2007	18:00	3.0	WSW
14-Nov-2007	19:00	3.0	W
14-Nov-2007	20:00	2.0	W
14-Nov-2007	21:00	3.0	WSW
14-Nov-2007	22:00	1.0	SW
14-Nov-2007	23:00	0.0	
15-Nov-2007	0:00	0.0	
15-Nov-2007	1:00	3.0	SW
15-Nov-2007	2:00	2.0	SW
15-Nov-2007	3:00	1.0	SW
15-Nov-2007	4:00	0.0	
15-Nov-2007	5:00	0.0	
15-Nov-2007	6:00	0.0	
15-Nov-2007	7:00	0.0	SE
15-Nov-2007	8:00	0.0	
15-Nov-2007	9:00	2.0	WNW
15-Nov-2007	10:00	4.0	WNW
15-Nov-2007	11:00	5.0	WNW
15-Nov-2007	12:00	6.0	WNW
15-Nov-2007	13:00	5.0	WNW
15-Nov-2007	14:00	4.0	WNW
15-Nov-2007	15:00	6.0	WNW
15-Nov-2007 15-Nov-2007	16:00	8.0	WNW
15-Nov-2007	17:00	8.0	WNW
			WNW
15-Nov-2007	18:00	6.0	W
15-Nov-2007	19:00	8.0	W
15-Nov-2007	20:00	7.0	
15-Nov-2007	21:00 22:00	3.0	SSW SSW
15-Nov-2007		3.0	
15-Nov-2007	23:00	1.0	SW
16-Nov-2007	0:00	0.0	
16-Nov-2007	1:00	1.0	SW
16-Nov-2007	2:00	0.0	SW
16-Nov-2007	3:00	0.0	SW
16-Nov-2007	4:00	0.0	
16-Nov-2007	5:00	0.0	SW
16-Nov-2007	6:00	0.0	
16-Nov-2007	7:00	0.0	
16-Nov-2007	8:00	1.0	WSW
16-Nov-2007	9:00	3.0	WNW
16-Nov-2007	10:00	6.0	W
16-Nov-2007	11:00	11.0	WNW
16-Nov-2007	12:00	11.0	WNW
16-Nov-2007	13:00	10.0	WNW
16-Nov-2007	14:00	8.0	WNW
16-Nov-2007	15:00	9.0	WNW
16-Nov-2007	16:00	4.0	WNW
16-Nov-2007	17:00	3.0	WNW

Date	Time	Wind Speed m/s	Direction
16-Nov-2007	18:00	2.0	WSW
16-Nov-2007	19:00	2.0	WSW
16-Nov-2007	20:00	0.0	SW
16-Nov-2007	21:00	0.0	SW
16-Nov-2007	22:00	2.0	SW
16-Nov-2007	23:00	3.0	NW
17-Nov-2007	0:00	7.0	SW
17-Nov-2007	1:00	7.0	W
17-Nov-2007	2:00	8.0	W
17-Nov-2007	3:00	8.0	W
17-Nov-2007	4:00	8.0	W
17-Nov-2007	5:00	7.0	W
17-Nov-2007	6:00	7.0	W
17-Nov-2007	7:00	7.0	W
17-Nov-2007	8:00	7.0	WNW
17-Nov-2007	9:00	9.0	W
17-Nov-2007	10:00	8.0	W
17-Nov-2007	11:00	8.0	WNW
17-Nov-2007	12:00	5.0	WNW
17-Nov-2007	13:00	5.0	WNW
17-Nov-2007	14:00	4.0	W
17-Nov-2007	15:00	4.0	W
17-Nov-2007	16:00	2.0	WNW
17-Nov-2007	17:00	2.0	SW
17-Nov-2007	18:00	2.0	SSW
17-Nov-2007	19:00	0.0	SSW
17-Nov-2007	20:00	3.0	W
17-Nov-2007	21:00	1.0	W
17-Nov-2007	22:00	2.0	W
17-Nov-2007	23:00	3.0	SW
18-Nov-2007	0:00	2.0	SW
18-Nov-2007	1:00	3.0	SSW
18-Nov-2007	2:00	3.0	W
18-Nov-2007	3:00	2.0	SW
18-Nov-2007	4:00	1.0	SSW
18-Nov-2007	5:00	2.0	SW
18-Nov-2007	6:00	6.0	W
18-Nov-2007	7:00	12.0	W
18-Nov-2007	8:00	8.0	W
18-Nov-2007	9:00	9.0	W
18-Nov-2007	10:00	12.0	WNW
18-Nov-2007	11:00	10.0	W
18-Nov-2007	12:00	12.0	WNW
18-Nov-2007	13:00	10.0	WNW
18-Nov-2007	14:00	10.0	WNW
18-Nov-2007	15:00	8.0	WNW
18-Nov-2007	16:00	8.0	WSW
18-Nov-2007	17:00	8.0	WSW
18-Nov-2007 18-Nov-2007			SW
	18:00	7.0	WSW
18-Nov-2007	19:00	7.0	
18-Nov-2007	20:00	6.0	WSW
18-Nov-2007	21:00	6.0	SW
18-Nov-2007	22:00	6.0	WSW
18-Nov-2007	23:00	7.0	SW

Date	Time	Wind Speed m/s	Direction
19-Nov-2007	0:00	7.0	WSW
19-Nov-2007	1:00	4.0	W
19-Nov-2007	2:00	5.0	WSW
19-Nov-2007	3:00	8.0	WNW
19-Nov-2007	4:00	8.0	WNW
19-Nov-2007	5:00	6.0	W
19-Nov-2007	6:00	2.0	SW
19-Nov-2007	7:00	4.0	SW
19-Nov-2007	8:00	3.0	WSW
19-Nov-2007	9:00	5.0	WSW
19-Nov-2007	10:00	6.0	WSW
19-Nov-2007	11:00	6.0	SW
19-Nov-2007	12:00	6.0	WNW
19-Nov-2007	13:00	6.0	WNW
19-Nov-2007	14:00	9.0	W
19-Nov-2007	15:00	8.0	W
19-Nov-2007	16:00	6.0	W
19-Nov-2007	17:00	2.0	W
19-Nov-2007	18:00	0.0	W
19-Nov-2007	19:00	0.0	
19-Nov-2007	20:00	1.0	S
19-Nov-2007	21:00	4.0	SW
19-Nov-2007	22:00	8.0	SW
19-Nov-2007	23:00	7.0	WSW
20-Nov-2007	0:00	4.0	SW
20-Nov-2007	1:00	4.0	W
20-Nov-2007	2:00	5.0	SW
20-Nov-2007	3:00	5.0	SW
20-Nov-2007	4:00	8.0	WNW
20-Nov-2007	5:00	6.0	SW
20-Nov-2007	6:00	8.0	SW
20-Nov-2007	7:00	5.0	WSW
20-Nov-2007	8:00	7.0	W
20-Nov-2007	9:00	12.0	WNW
20-Nov-2007	10:00	13.0	WNW
20-Nov-2007	11:00	11.0	WNW
20-Nov-2007	12:00	8.0	WNW
20-Nov-2007	13:00	6.0	W
20-Nov-2007	14:00	4.0	WNW
20-Nov-2007	15:00	6.0	W
20-Nov-2007	16:00	5.0	W
20-Nov-2007	17:00	4.0	W
20-Nov-2007	18:00	0.0	WSW
20-Nov-2007	19:00	0.0	
20-Nov-2007	20:00	0.0	
20-Nov-2007	21:00	0.0	
20-Nov-2007	22:00	0.0	
20-Nov-2007	23:00	0.0	
21-Nov-2007	0:00	0.0	
21-Nov-2007	1:00	0.0	
21-Nov-2007	2:00	1.0	WSW
21-Nov-2007	3:00	2.0	SW
21-Nov-2007	4:00	4.0	W
	1.00	1.0	* *

Date	Time	Wind Speed m/s	Direction
21-Nov-2007	6:00	2.0	W
21-Nov-2007	7:00	2.0	W
21-Nov-2007	8:00	5.0	W
21-Nov-2007	9:00	6.0	W
21-Nov-2007	10:00	8.0	W
21-Nov-2007	11:00	10.0	WNW
21-Nov-2007	12:00	9.0	W
21-Nov-2007	13:00	8.0	W
21-Nov-2007	14:00	7.0	W
21-Nov-2007	15:00	8.0	W
21-Nov-2007	16:00	5.0	WSW
21-Nov-2007	17:00	5.0	WSW
21-Nov-2007	18:00	2.0	WSW
21-Nov-2007	19:00	3.0	W
21-Nov-2007	20:00	3.0	WSW
21-Nov-2007	21:00	1.0	NW
21-Nov-2007	22:00	3.0	SW
21-Nov-2007	23:00	5.0	WNW
22-Nov-2007	0:00	9.0	WNW
22-Nov-2007	1:00	9.0	W
22-Nov-2007	2:00	4.0	WNW
22-Nov-2007	3:00	1.0	SSW
22-Nov-2007	4:00	2.0	SSW
22-Nov-2007	5:00	3.0	SSW
22-Nov-2007	6:00	5.0	SW
22-Nov-2007	7:00	6.0	WSW
22-Nov-2007	8:00	5.0	WNW
22-Nov-2007 22-Nov-2007	9:00	3.0	WSW
22-Nov-2007 22-Nov-2007	10:00	5.0	WNW
22-Nov-2007	11:00	7.0	WNW
22-Nov-2007 22-Nov-2007	12:00	9.0	WNW
22-Nov-2007 22-Nov-2007	13:00	8.0	W
22-Nov-2007 22-Nov-2007	14:00	5.0	WSW
22-Nov-2007 22-Nov-2007	15:00	6.0	SW
22-Nov-2007 22-Nov-2007	16:00	3.0	WSW
22-Nov-2007 22-Nov-2007	17:00	5.0	W
22-Nov-2007 22-Nov-2007	18:00	5.0	W
22-Nov-2007 22-Nov-2007	19:00	4.0	W
22-Nov-2007 22-Nov-2007	20:00	3.0	VV
22-Nov-2007 22-Nov-2007	21:00	1.0	W
	22:00	2.0	W
22-Nov-2007	23:00	1.0	NW
22-Nov-2007			W
23-Nov-2007	0:00	2.0	WSW
23-Nov-2007	1:00	3.0	WSW
23-Nov-2007	2:00	6.0	W
23-Nov-2007	3:00	1.0	
23-Nov-2007	4:00	3.0	SW
23-Nov-2007	5:00	3.0	SW
23-Nov-2007	6:00	4.0	SW
23-Nov-2007	7:00	2.0	WSW
23-Nov-2007	8:00	4.0	WNW
23-Nov-2007	9:00	7.0	WNW
23-Nov-2007	10:00	7.0	WNW
23-Nov-2007	11:00	7.0	W

Date	Time	Wind Speed m/s	Direction
23-Nov-2007	12:00	7.0	SW
23-Nov-2007	13:00	6.0	SW
23-Nov-2007	14:00	8.0	W
23-Nov-2007	15:00	7.0	WNW
23-Nov-2007	16:00	4.0	WNW
23-Nov-2007	17:00	5.0	W
23-Nov-2007	18:00	2.0	W
23-Nov-2007	19:00	0.0	SSW
23-Nov-2007	20:00	0.0	
23-Nov-2007	21:00	0.0	
23-Nov-2007	22:00	2.0	WNW
23-Nov-2007	23:00	3.0	W
24-Nov-2007	0:00	3.0	SSW
24-Nov-2007	1:00	2.0	SSW
24-Nov-2007	2:00	0.0	SSW
24-Nov-2007	3:00	0.0	
24-Nov-2007	4:00	0.0	
24-Nov-2007	5:00	2.0	WSW
24-Nov-2007	6:00	2.0	W
24-Nov-2007	7:00	0.0	WNW
24-Nov-2007	8:00	2.0	SW
24-Nov-2007	9:00	6.0	SW
24-Nov-2007	10:00	9.0	WNW
24-Nov-2007	11:00	9.0	W
24-Nov-2007	12:00	8.0	WSW
24-Nov-2007	13:00	8.0	SW
24-Nov-2007	14:00	7.0	WSW
24-Nov-2007	15:00	5.0	SW
24-Nov-2007	16:00	7.0	W
24-Nov-2007	17:00	5.0	W
24-Nov-2007	18:00	5.0	WNW
24-Nov-2007	19:00	3.0	WNW
24-Nov-2007	20:00	3.0	WSW
24-Nov-2007	21:00	2.0	SSW
24-Nov-2007	22:00	2.0	SW
24-Nov-2007	23:00	2.0	SSW
25-Nov-2007	0:00	3.0	W
25-Nov-2007	1:00	1.0	WNW
25-Nov-2007	2:00	0.0	WSW
25-Nov-2007 25-Nov-2007	3:00	0.0	
25-Nov-2007	4:00	0.0	
25-Nov-2007 25-Nov-2007	5:00	0.0	
25-Nov-2007 25-Nov-2007	6:00	0.0	
25-Nov-2007 25-Nov-2007	7:00	0.0	
25-Nov-2007 25-Nov-2007	8:00	0.0	
25-Nov-2007 25-Nov-2007	9:00	0.0	WSW
25-Nov-2007 25-Nov-2007	10:00	4.0	WNW
25-Nov-2007 25-Nov-2007	11:00	6.0	W
			SW
25-Nov-2007	12:00	7.0	
25-Nov-2007	13:00	8.0	W
25-Nov-2007	14:00	3.0	W
25-Nov-2007	15:00	3.0	WSW
25-Nov-2007	16:00	1.0	SSW
25-Nov-2007	17:00	0.0	SSW

Date	Time	Wind Speed m/s	Direction
25-Nov-2007	18:00	1.0	SW
25-Nov-2007	19:00	1.0	SSW
25-Nov-2007	20:00	1.0	SSW
25-Nov-2007	21:00	4.0	SW
25-Nov-2007	22:00	5.0	SW
25-Nov-2007	23:00	7.0	WSW
26-Nov-2007	0:00	5.0	W
26-Nov-2007	1:00	4.0	WNW
26-Nov-2007	2:00	6.0	WSW
26-Nov-2007	3:00	5.0	WSW
26-Nov-2007	4:00	6.0	WNW
26-Nov-2007	5:00	4.0	WNW
26-Nov-2007	6:00	4.0	WSW
26-Nov-2007	7:00	2.0	WSW
26-Nov-2007	8:00	6.0	WSW
26-Nov-2007	9:00	7.0	WSW
26-Nov-2007	10:00	7.0	WSW
26-Nov-2007	11:00	5.0	SW
26-Nov-2007	12:00	9.0	WSW
26-Nov-2007	13:00	7.0	SW
26-Nov-2007	14:00	6.0	WSW
26-Nov-2007	15:00	7.0	SW
26-Nov-2007	16:00	6.0	SW
26-Nov-2007	17:00	5.0	W
26-Nov-2007	18:00	5.0	W
26-Nov-2007	19:00	10.0	WSW
26-Nov-2007	20:00	8.0	WSW
26-Nov-2007	21:00	7.0	W
26-Nov-2007	22:00	10.0	WSW
26-Nov-2007	23:00	8.0	WSW
27-Nov-2007	0:00	12.0	WSW
27-Nov-2007	1:00	10.0	WSW
27-Nov-2007	2:00	10.0	WSW
27-Nov-2007 27-Nov-2007	3:00	6.0	W
27-Nov-2007 27-Nov-2007	4:00	7.0	WSW
27-Nov-2007 27-Nov-2007	5:00	14.0	WSW
27-Nov-2007 27-Nov-2007	6:00	13.0	WSW
27-Nov-2007 27-Nov-2007	7:00	7.0	WSW
27-Nov-2007 27-Nov-2007	8:00	10.0	WSW
27-Nov-2007 27-Nov-2007	9:00	13.0	WSW
	10:00	14.0	WSW
27-Nov-2007 27-Nov-2007		15.0	WSW
	11:00		W
27-Nov-2007	12:00	7.0	W
27-Nov-2007	13:00 14:00	3.0	W
27-Nov-2007 27-Nov-2007			SSW
	15:00 16:00	4.0	
27-Nov-2007	16:00	4.0	WSW
27-Nov-2007	17:00	2.0	WSW
27-Nov-2007	18:00	2.0	SW
27-Nov-2007	19:00	3.0	SW
27-Nov-2007	20:00	2.0	WSW
07 NL 0007			
27-Nov-2007 27-Nov-2007	21:00 22:00	3.0	SSW WSW

Date	Time	Wind Speed m/s	Direction		
28-Nov-2007	0:00	5.0	WSW		
28-Nov-2007	1:00	2.0	SW		
28-Nov-2007	2:00	3.0	SW		
28-Nov-2007	3:00	2.0	SW		
28-Nov-2007	4:00	2.0	WSW		
28-Nov-2007	5:00	4.0	SW		
28-Nov-2007	6:00	2.0	W		
28-Nov-2007	7:00	4.0	WSW		
28-Nov-2007	8:00	6.0	SW		
28-Nov-2007	9:00	6.0	W		
28-Nov-2007	10:00	6.0	WSW		
28-Nov-2007	11:00	6.0	WSW		
28-Nov-2007	12:00	7.0	W		
28-Nov-2007	13:00	4.0	WNW		
28-Nov-2007	14:00	5.0	WSW		
28-Nov-2007	15:00	4.0	W		
28-Nov-2007	16:00	4.0	WSW		
28-Nov-2007	17:00	1.0	SSW		
28-Nov-2007	18:00	0.0	SW		
28-Nov-2007	19:00	1.0	SSW		
28-Nov-2007 28-Nov-2007	20:00	1.0	SW		
28-Nov-2007	21:00	1.0	SW		
28-Nov-2007	22:00	4.0	SW		
	23:00	5.0	SW		
28-Nov-2007 29-Nov-2007	0:00	4.0	SW		
	1:00	3.0	SW		
29-Nov-2007 29-Nov-2007	2:00	1.0	SW		
29-Nov-2007 29-Nov-2007			SW		
	3:00	0.0			
29-Nov-2007	4:00	0.0			
29-Nov-2007	5:00	0.0			
29-Nov-2007	6:00	0.0			
29-Nov-2007	7:00	0.0			
29-Nov-2007	8:00	0.0			
29-Nov-2007	9:00	1.0	W		
29-Nov-2007	10:00	7.0	WNW		
29-Nov-2007	11:00	9.0	W		
29-Nov-2007	12:00	7.0	W		
29-Nov-2007	13:00	7.0	WNW		
29-Nov-2007	14:00	8.0	WNW		
29-Nov-2007	15:00	6.0	W		
29-Nov-2007	16:00	4.0	W		
29-Nov-2007	17:00	1.0	WNW		
29-Nov-2007	18:00	0.0	ENE		
29-Nov-2007	19:00	0.0			
29-Nov-2007	20:00	0.0			
29-Nov-2007	21:00	0.0			
29-Nov-2007	22:00	0.0			
29-Nov-2007	23:00	0.0			
30-Nov-2007	0:00	0.0			
30-Nov-2007	1:00	0.0			
30-Nov-2007	2:00	0.0			
30-Nov-2007	3:00	0.0			
30-Nov-2007	4:00	0.0			
30-Nov-2007	5:00	0.0			

Date	Time	Wind Speed m/s	Direction
30-Nov-2007	6:00	0.0	
30-Nov-2007	7:00	0.0	
30-Nov-2007	8:00	0.0	
30-Nov-2007	9:00	0.0	
30-Nov-2007	10:00	1.0	W
30-Nov-2007	11:00	6.0	WNW
30-Nov-2007	12:00	5.0	WNW
30-Nov-2007	13:00	6.0	WNW
30-Nov-2007	14:00	6.0	WNW
30-Nov-2007	15:00	5.0	NW
30-Nov-2007	16:00	7.0	W
30-Nov-2007	17:00	6.0	W
30-Nov-2007	18:00	3.0	WNW
30-Nov-2007	19:00	1.0	WSW
30-Nov-2007	20:00	0.0	SW
30-Nov-2007	21:00	0.0	
30-Nov-2007	22:00	0.0	
30-Nov-2007	23:00	0.0	

APPENDIX E 1-HOUR TSP MONITORING RESULTS AND GRAPHICAL PRESENTATION

Appendix E - 1-hour TSP Monitoring Results


Location AM 3 - Garden Villa


Date	Weather	Filter We	eight (g)	Flow Rate	e (m³/min.)	Elaps	e Time	Air	Atmospheric	Particulate	Av. flow	Total vol.	Sampling	Conc.
	Condition	Initial	Final	Initial	Final	Initial	Final	Temp. (K)	Pressure(Pa)	weight(g)	(m ³ /min)	(m^3)	Time(hrs.)	$(\mu g/m^3)$
1-Nov-07	Cloudy	2.8172	2.8302	1.24	1.24	6583.0	6584.0	291.9	767.1	0.0130	1.24	74.6	1.0	174.3
5-Nov-07	Sunny	2.8345	2.8444	1.24	1.24	6608.0	6609.0	293.5	765.2	0.0099	1.24	74.3	1.0	133.3
6-Nov-07	Sunny	2.8426	2.8545	1.24	1.24	6609.0	6610.0	294.1	764.0	0.0119	1.24	74.2	1.0	160.5
8-Nov-07	Sunny	2.8185	2.8301	1.24	1.24	6610.0	6611.0	291.2	763.7	0.0116	1.24	74.5	1.0	155.7
12-Nov-07	Sunny	2.8009	2.8106	1.24	1.24	6635.0	6636.0	293.8	766.5	0.0097	1.24	74.3	1.0	130.5
13-Nov-07	Sunny	2.7895	2.7968	1.24	1.24	6636.0	6637.0	294.2	766.3	0.0073	1.24	74.3	1.0	98.3
16-Nov-07	Sunny	2.8199	2.8268	1.23	1.23	6661.0	6662.0	299.1	765.6	0.0069	1.23	73.6	1.0	93.8
19-Nov-07	Sunny	2.8028	2.8151	1.25	1.25	6662.0	6663.0	291.7	769.9	0.0123	1.25	74.8	1.0	164.5
20-Nov-07	Sunny	2.8256	2.8337	1.25	1.25	6663.0	6664.0	291.9	769.7	0.0081	1.25	74.7	1.0	108.4
22-Nov-07	Sunny	2.8146	2.8267	1.23	1.23	6688.0	6689.0	296.2	766.2	0.0121	1.23	74.0	1.0	163.6
26-Nov-07	Sunny	2.8254	2.8358	1.23	1.23	6689.0	6690.0	294.6	764.4	0.0104	1.23	74.1	1.0	140.4
28-Nov-07	Sunny	2.8340	2.8537	1.22	1.22	6714.0	6715.0	292.6	763.3	0.0197	1.22	73.3	1.0	268.6
29-Nov-07	Sunny	2.8306	2.8476	1.23	1.23	6714.0	6715.0	289.5	769.7	0.0170	1.23	74.0	1.0	229.9
													Min	93.8
													Max	268.6
													Average	155.5

Location AM 4 - Government Quarters

Date	Weather	Filter We	eight (g)	Flow Rate	e (m³/min.)	Elaps	se Time	Air	Atmospheric	Particulate	Av. flow	Total vol.	Sampling	Conc.
	Condition	Initial	Final	Initial	Final	Initial	Final	Temp. (K)	Pressure(Pa)	weight(g)	(m ³ /min)	(m^3)	Time(hrs.)	$(\mu g/m^3)$
1-Nov-07	Cloudy	2.8208	2.8274	1.24	1.24	6618.5	6619.5	291.9	767.1	0.0066	1.24	74.4	1.0	88.8
5-Nov-07	Sunny	2.8341	2.8426	1.23	1.23	6643.5	6644.5	293.5	765.2	0.0085	1.23	74.1	1.0	114.8
6-Nov-07	Sunny	2.8488	2.8574	1.23	1.23	6644.5	6645.5	294.1	764.0	0.0086	1.23	73.9	1.0	116.3
8-Nov-07	Sunny	2.7986	2.8075	1.24	1.24	6645.5	6646.5	291.2	763.7	0.0089	1.24	74.3	1.0	119.8
12-Nov-07	Sunny	2.8468	2.8546	1.21	1.21	6670.5	6671.5	294.0	766.3	0.0078	1.21	72.8	1.0	107.2
13-Nov-07	Sunny	2.8339	2.8360	1.21	1.21	6671.5	6672.5	294.2	766.3	0.0021	1.21	72.7	1.0	28.9
16-Nov-07	Sunny	2.8327	2.8338	1.20	1.20	6696.5	6697.5	298.9	765.7	0.0011	1.20	72.2	1.0	15.2
19-Nov-07	Sunny	2.8223	2.8317	1.22	1.22	6697.5	6698.5	291.7	769.9	0.0094	1.22	73.1	1.0	128.5
20-Nov-07	Sunny	2.8004	2.8027	1.22	1.22	6698.5	6699.5	291.9	769.7	0.0023	1.22	73.1	1.0	31.5
22-Nov-07	Sunny	2.7822	2.7905	1.21	1.21	6723.5	6724.5	296.2	766.2	0.0083	1.21	72.5	1.0	114.5
26-Nov-07	Sunny	2.8147	2.8258	1.21	1.21	6724.5	6725.5	294.6	764.4	0.0111	1.21	72.6	1.0	152.9
28-Nov-07	Sunny	2.8178	2.8265	1.20	1.20	6749.5	6750.5	297.7	765.4	0.0087	1.20	72.3	1.0	120.3
29-Nov-07	Sunny	2.8227	2.8382	1.22	1.22	6749.5	6750.5	289.5	769.7	0.0155	1.22	73.4	1.0	211.3
													Min	15.2
													Max	211.3
													Average	103.9

1-hr TSP Levels

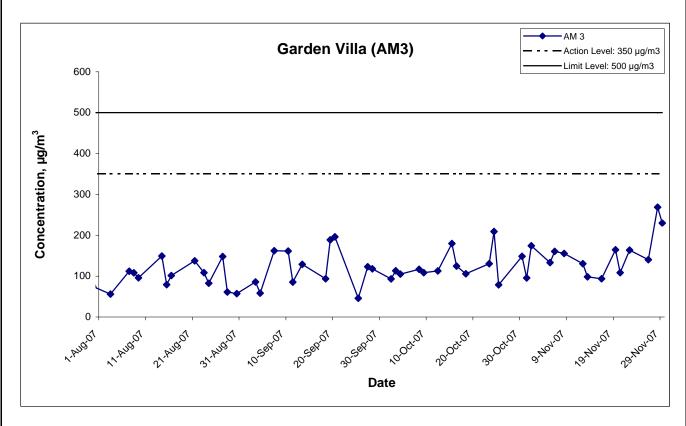

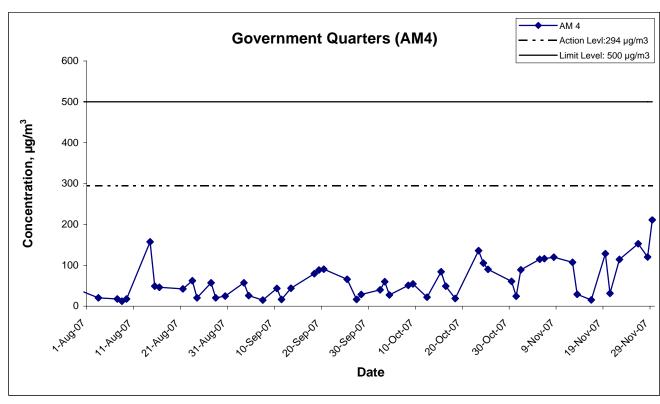

Route 8 (previously known as Route 9) between Cheung Sha Wan & Sha Tin Contract HY/2003/02 - Eagle's Nest Tunnel and Associated Works Graphical Presentation of 1-hour TSP Impact Monitoring

Results

Title

Ε

Nov 07



APPENDIX F 24-HOUR TSP MONITORING RESULTS AND GRAPHICAL PRESENTATION

Appendix F - 24-hour TSP Monitoring Results


Location AM 3 - Garden Villa


Date	Weather	Filter W	eight (g)	Flow Rate	e (m³/min.)	Elaps	e Time	Air	Atmospheric	Particulate	Av. flow	Total vol.	Sampling	Conc.
	Condition	Initial	Final	Initial	Final	Initial	Final	Temp. (K)	Pressure(Pa)	weight(g)	(m ³ /min)	(m ³)	Time(hrs.)	$(\mu g/m^3)$
3-Nov-07	Sunny	2.8095	2.9349	1.24	1.24	6584.0	6608.0	291.9	767.1	0.1254	1.24	1790.3	24.0	70.0
9-Nov-07	Sunny	2.8320	2.9569	1.23	1.23	6611.0	6635.0	295.2	764.4	0.1249	1.23	1776.4	24.0	70.3
15-Nov-07	Sunny	2.8331	2.9340	1.24	1.24	6637.0	6661.0	295.6	767.3	0.1009	1.24	1778.9	24.0	56.7
21-Nov-07	Sunny	2.8146	2.9341	1.25	1.25	6664.0	6688.0	291.8	769.7	0.1195	1.25	1793.8	24.0	66.6
27-Nov-07	Sunny	2.8011	2.9684	1.22	1.22	6690.0	6714.0	291.6	763.9	0.1673	1.22	1763.3	24.0	94.9
													Min	56.7
													Max	94.9
													Average	71.7

Location AM 4 - Government Quarters

Date	Weather	Filter W	eight (g)	Flow Rate (m ³ /min.)		te (m³/min.) Elapse Time		Air	Atmospheric	Particulate	Av. flow	Total vol.	Sampling	Conc.
	Condition	Initial	Final	Initial	Final	Initial	Final	Temp. (K)	Pressure(Pa)	weight(g)	(m ³ /min)	(m^3)	Time(hrs.)	$(\mu g/m^3)$
3-Nov-07	Sunny	2.8012	2.8255	1.24	1.24	6619.5	6643.5	291.9	767.1	0.0243	1.24	1782.2	24.0	13.6
9-Nov-07	Sunny	2.7878	2.8088	1.23	1.23	6646.5	6670.5	295.2	764.4	0.0210	1.23	1771.8	24.0	11.9
15-Nov-07	Sunny	2.8095	2.8357	1.21	1.21	6672.5	6696.5	295.4	767.5	0.0262	1.21	1743.0	24.0	15.0
21-Nov-07	Sunny	2.8165	2.8654	1.22	1.22	6699.5	6723.5	291.8	769.7	0.0489	1.22	1754.5	24.0	27.9
27-Nov-07	Sunny	2.8079	2.8824	1.22	1.22	6725.5	6749.5	291.6	763.9	0.0745	1.22	1749.3	24.0	42.6
													Min	11.9
													Max	42.6
													Average	22.2

24-hr TSP Levels

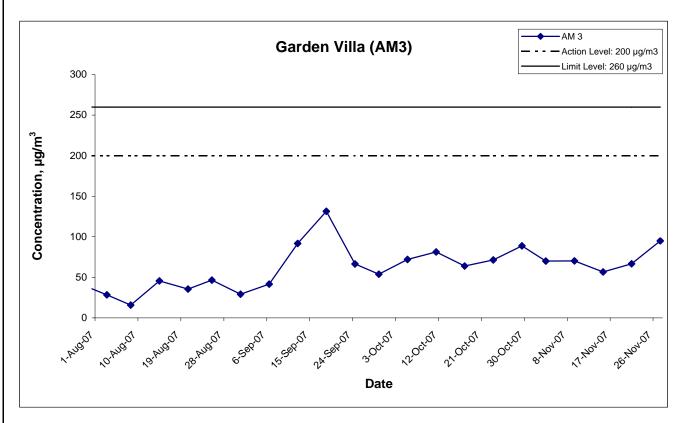

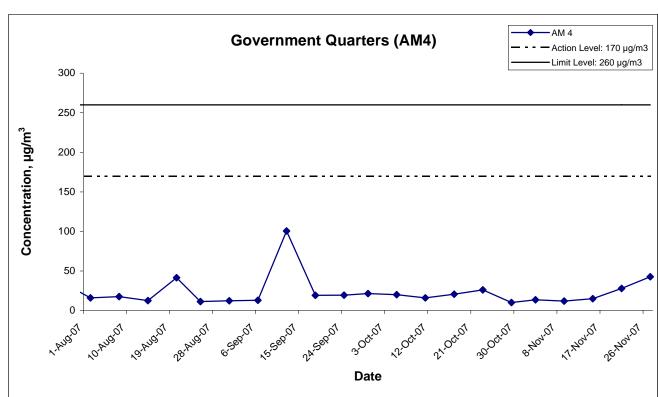

Route 8 (previously known as Route 9) between Cheung Sha Wan & Sha Tin Contract HY/2003/02 - Eagle's Nest Tunnel and Associated Works Graphical Presentation of 24-hour TSP Impact Monitoring

Results

Title

Scale		Project	
	N.T.S	No.	MA3024
Date		Append	ix

Nov 07



APPENDIX G NOISE MONITORING RESULTS AND GRAPHICAL PRESENTATION

Appendix G - Noise Monitoring Results

Location NM	Location NM5 - Villa Carlton												
						Unit: dB (A) (30	-min)						
Date	Time	Weather	Measured Noise Level			Baseline Level	Construction Noise Level	Remarks					
			L _{eq}	L ₁₀	L 90	L _{eq}	L _{eq}						
1-Nov-07	14:00	Cloudy	74.6	78.0	71.5		74.6, Measured [Baseline						
8-Nov-07	9:00	Sunny	68.3	71.5	64.0		68.3, Measured [Baseline	The major noise source					
16-Nov-07	13:50	Fine	77.6	79.0	74.5	77.1	68.0	was identified as traffic					
22-Nov-07	13:00	Sunny	76.7	79.0	75.0		76.7, Measured [Baseline	noise from Tai Po Road.					
29-Nov-07	14:57	Sunny	68.4	70.5	64.5	1	68.4, Measured [Baseline	1					

Location NM	Location NM6 - Government Quarters												
Date	Time	Weather		(A) (30- red Nois		Remarks							
			L _{eq}	L ₁₀	L 90								
1-Nov-07	13:00	Cloudy	62.3	65.5	58.0								
8-Nov-07	10:10	Sunny	54.2	59.5	51.0								
16-Nov-07	13:10	Fine	62.4	63.5	57.0	-							
22-Nov-07	13:40	Sunny	55.8	56.5	50.5								
29-Nov-07	14:07	Sunny	56.4	58.0	52.0								

Location NM	7 - Gard	en Vilia						
					·min)			
Date	Time	Weather	Measu	red Nois	e Level	Baseline Level	Construction Noise Level	Remarks
			L _{eq}	L ₁₀	L 90	L _{eq}	L _{eq}	
1-Nov-07	15:30	Cloudy	64.2	68.0	62.0		62.6	
8-Nov-07	15:00	Sunny	60.0	64.0	57.5		53.1	
16-Nov-07	14:00	Sunny	64.2	69.0	61.0	59.0	62.6	-
22-Nov-07	9:30	Sunny	67.1	70.0	64.5		66.4	
29-Nov-07	16:00	Sunny	63.2	66.0	60.5		61.1	

Appendix G - Noise Monitoring Results

Restricted Hours - 19:00 to 23:00 on normal weekdays

Location NM	5 - Villa	Carlton							
Data	T:	\\/		dB (A) (5-min)		nin)	Baseline Level	Construction Noise Level	
Date	Time	Weather	L _{eq}	L ₁₀	L 90	Average L _{eq}	L _{eq}	L _{eq}	Remarks
	20:20		74.6	76.0	71.0				
1-Nov-07	20:25	Cloudy	73.8	76.0	71.0	74.1		74.1, Measured [Baseline	
	20:30		73.9	76.0	71.0				
	20:30		73.0	75.5	70.0				1
8-Nov-07	20:35	Cloudy	73.2	76.0	70.0	73.2		73.2, Measured [Baseline	
	20:40		73.3	76.0	70.0				
	20:30		71.6	76.0	69.5				The major noise source
16-Nov-07	20:35	Cloudy	72.5	76.5	69.5	72.2	75.8	72.2, Measured [Baseline	was identified as traffic
	20:40		72.5	76.5	69.5				noise from Tai Po Road.
	20:15		73.2	75.5	69.0				1
22-Nov-07	20:20	Cloudy	73.6	76.0	69.5	73.4		73.4, Measured [Baseline	
	20:25		73.3	75.5	69.0				
	20:20		74.1	78.5	71.5				1
29-Nov-07	20:25	Cloudy	74.7	79.0	72.0	74.3		74.3, Measured [Baseline	
	20:30		74.0	78.5	71.5				

Location NM	6 - Gove	rnment Qua	rters						
Doto	Time	Weather	dB (A) (5-min)			nin)	Baseline Level	Baseline Level Construction Noise Level	
Date	Time	vveamer	L _{eq}	L ₁₀	L 90	Average L _{eq}	L _{eq}	L _{eq}	Remarks
	19:45		56.0	58.0	51.5				
1-Nov-07	19:50	Cloudy	55.6	58.0	51.0	55.8		55.8, Measured [Baseline	
	19:55		55.8	58.0	51.0				
	19:45		54.6	57.0	51.0				
8-Nov-07	19:50	Cloudy	54.5	57.0	51.0	54.6		54.6, Measured [Baseline	
	19:55		54.6	57.0	51.0				
	19:45		54.3	58.5	50.5				
16-Nov-07	19:50	Cloudy	54.5	58.5	50.5	54.3	56.1	54.3, Measured [Baseline	-
	19:55		54.0	58.0	50.5				
	19:45		54.0	58.5	51.5				
22-Nov-07	19:50	Cloudy	53.6	58.0	51.0	53.8		53.8, Measured [Baseline	
	19:55		53.7	58.0	51.0				
•	19:45		52.5	56.0	47.5				
29-Nov-07	19:50	Cloudy	52.3	56.0	47.0	52.3		52.3, Measured [Baseline	
	19:55		52.0	55.5	47.0				

Location NM	7 - Gard	en Villa							
Date	Time	Weather		dB	(A) (5-m	nin)	Baseline Level	Construction Noise Level	
Date	Time	vveatrier	L _{eq}	L ₁₀	L 90	Average L _{eq}	L _{eq}	L _{eq}	Remarks
	19:00		56.6	59.0	52.0				
1-Nov-07	19:05	Cloudy	56.0	58.5	52.0	56.4		56.4, Measured [Baseline	
	19:10		56.6	59.0	52.0				
	19:00		56.7	59.0	52.5				
8-Nov-07	19:05	Cloudy	56.3	59.0	0 52.5 56.5		56.5, Measured [Baseline		
	19:10		56.6	59.0	52.5				
	19:00		56.8	59.5	52.0				The major noise source
16-Nov-07	19:05	Cloudy	56.6	59.5	52.0	56.7	58.3	56.7, Measured [Baseline	was identified as traffic
	19:10		56.6	59.5	52.0				noise from Tai Po Road.
	19:00		56.4	59.0	52.0				
22-Nov-07	19:05	Cloudy	56.5	59.0	52.0	56.5		56.5, Measured [Baseline	
	19:10		56.7	59.0	52.0				
	19:00		55.9	59.5	52.5				
29-Nov-07	19:05	Cloudy	56.3	59.5	53.0	56.1		56.1, Measured [Baseline	
	19:10		56.0	59.5	53.0				

[#] Construction Noise Level (Leq) = Measured Noise Level (Leq) - Baseline Noise Level (Leq)

^{*}Bolded value indicated limit level exceedance

Appendix G - Noise Monitoring Results

Restricted Hours - 23:00 to 07:00 on normal weekdays


Location NM	5 - Villa	Carlton							
Data	Data Time Weather		dB (A) (5-min)				Baseline Level	Construction Noise Level	
Date	Time	Weather	L _{eq}	L ₁₀	L 90	Average L _{eq}	L _{eq}	L _{eq}	Remarks
	23:00		72.8	75.5	69.5				
1-Nov-07	23:05	Cloudy	72.4	75.0	69.0	72.4		72.4, Measured [Baseline	
	23:10		72.1	75.0	69.0				
	23:00		73.0	77.0	68.5				1
8-Nov-07	23:05	Cloudy	72.8	77.0	68.5	72.8		72.8, Measured [Baseline	
	23:10		72.5	77.0	68.5				
	23:00		72.8	76.5	69.5				The major noise source
16-Nov-07	23:05	Cloudy	72.0	76.0	69.0	72.3	74.3	72.3, Measured [Baseline	was identified as traffic
	23:10		72.1	76.0	69.0				noise from Tai Po Road.
	23:00		72.8	75.0	68.5				1
22-Nov-07	23:05	Cloudy	72.3	75.0	68.0	72.5		72.5, Measured [Baseline	
	23:10		72.4	75.0	68.5				
	23:00		72.6	75.5	69.5	_			
29-Nov-07	23:05	Cloudy	72.8	75.5	69.5	72.6		72.6, Measured [Baseline	
	23:10		72.5	75.5	69.5				


Location NM	6 - Gove	rnment Qua	rters						
Doto	Time	Moothor	dB (A) (5-min)			nin)	Baseline Level	Construction Noise Level	
Date	Time	Weather	L _{eq}	L ₁₀	L 90	Average L _{eq}	L _{eq}	L _{eq}	Remarks
	23:25		49.8	53.0	46.5				
1-Nov-07	23:30	Cloudy	49.7	53.0	46.5	49.9		49.9, Measured [Baseline	
	23:35		50.2	53.5	46.5				
	23:25		50.3	53.5	47.5				The noise monitoring
8-Nov-07	23:30	Cloudy	50.6	54.0	47.5	50.6		50.6, Measured [Baseline	results are well within the
	23:35		50.8	54.0	47.5				range of Baseline
	23:25		50.0	54.0	47.5				Monitoring Level and
16-Nov-07	23:30	Cloudy	50.2	54.0	47.5	50.1	52.8	50.1, Measured [Baseline	there is no evidence
	23:35		50.2	54.0	47.5				showing that the
	23:25		51.3	53.5	47.0				dominant noise was
22-Nov-07	23:30	Cloudy	51.2	53.0	47.0	51.3		51.3, Measured [Baseline	generated from the
	23:35		51.5	53.5	47.5				construction activities.
	23:25		51.2	55.0	47.5				
29-Nov-07	23:30	Cloudy	51.8	55.0	47.5	51.5		51.5, Measured [Baseline	
	23:35		51.5	55.0	47.5				


Location NM	17 - Gard	en Villa							
Date	Time	Weather	dB (A) (5-min)		in)	Baseline Level	Construction Noise Level		
Date	Time	Weather	L _{eq}	L ₁₀	L 90	Average L _{eq}	L _{eq}	L _{eq}	Remarks
	23:50		55.3	59.0	52.0				
1-Nov-07	23:55	Cloudy	55.2	59.0	52.0	55.2		55.2, Measured [Baseline	
	0:00		55.0	59.0	52.0				
	23:50		53.7	58.0	49.5				
8-Nov-07	23:55	Cloudy	53.2	57.5	49.0	53.3		53.3, Measured [Baseline	
	0:00		53.0	57.5	49.0				
	23:50		54.3	58.0	51.5				The major noise source
16-Nov-07	23:55	Cloudy	54.2	58.0	51.5	54.4	56.5	54.4, Measured [Baseline	was identified as traffic
	0:00		54.6	58.5	52.0				noise from Tai Po Road.
	23:50		53.6	58.0	50.0				
22-Nov-07	23:55	Cloudy	53.6	58.0	50.0	53.7		53.7, Measured [Baseline	
	0:00		53.9	58.5	50.5				
	23:50		54.4	59.5	52.0				
29-Nov-07	23:55	Cloudy	54.1	59.0	52.0	54.2		54.2, Measured [Baseline	
	0:00		54.1	59.0	52.0				

[#] Construction Noise Level (Leq) = Measured Noise Level (Leq) - Baseline Noise Level (Leq)

^{*}Bolded value indicated limit level exceedance

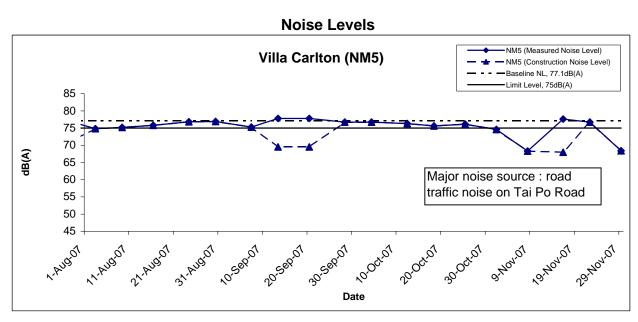

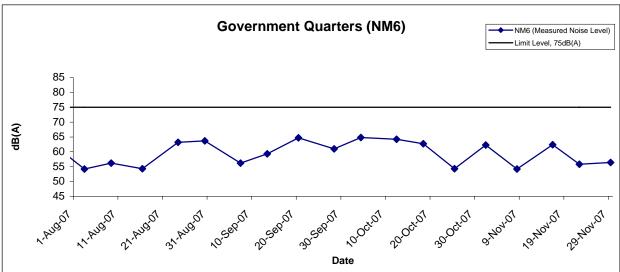

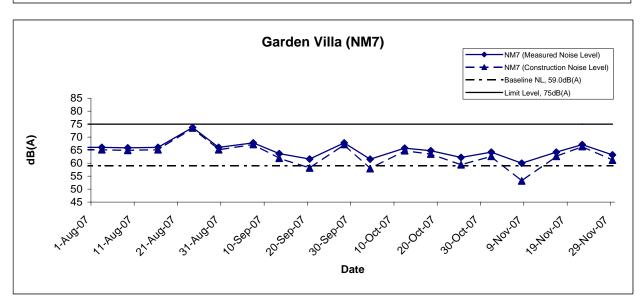

* Construction Noise Level = Measured Noise Level - Baseline Level (If the measured noise level is lower than the baseline level, the construction noise level will be taken as the measured one)

Title
Route 8 (previously known as Route 9) between Cheung Sha Wan & Sha Tin
Contract HY/2003/02 - Eagle's Nest Tunnel and Associated Works


Graphical Presentation of Construction Noise Monitoring Results


_	COHST	action nois	S ICVCI WIII DC LANC
	Scale		Project
		N.T.S	No. MA3024
	Date	Nov 07	Appendix G




Restricted Hours (19:00 to 23:00) - Noise Levels NM5 (Construction Noise Level) Villa Carlton (NM5) Limit Level, 70 dB(A) NM5 (Measured Noise Level) -Baseline NL, 75.8dB(A) 85 80 75 70 65 60 55 50 Major noise source : 45 road traffic noise 40 35 Date NM6 (Construction Noise Level) **Government Quarters (NM6)** Limit Level, 65 dB(A) NM6 (Measured Noise Level) 85 -Baseline NL, 56.1dB(A) 80 75 70 65 60 55 50 45 40 35 NO-OCT-OT Date NM7 (Construction Noise Level) Garden Villa (NM7) Limit Level, 60 dB(A) NM7 (Measured Noise Level) 85 -Baseline NL, 58.3dB(A) 80 75 Major noise source : 70 road traffic noise 65 60 55 50 45 40 35 Construction Noise Level = Measured Noise Level - Baseline Level (If the measured noise level is lower than the baseline level, the construction noise level will be taken as the measured one) Title Scale Project Route 8 (previously known as Route 9) between Cheung Sha Wan & Sha Tin Contract HY/2003/02 - Eagle's Nest Tunnel and Associated Works N.T.S MA3024 Appendix Date **Graphical Presentation of Construction Noise Monitoring** Nov 07 G Results

Restricted Hours (23:00 to 07:00) - Noise Levels

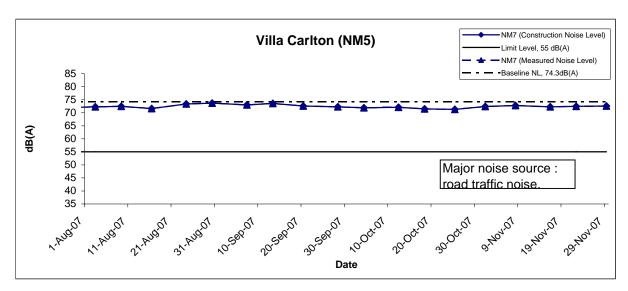

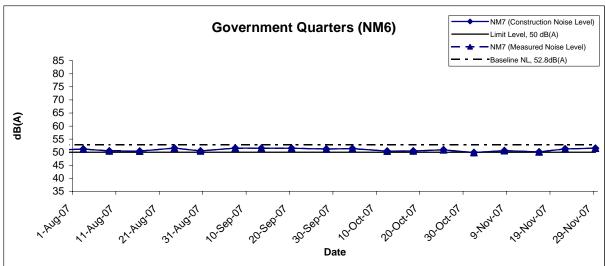

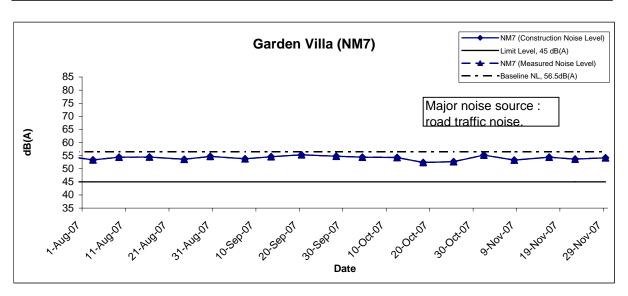

* Construction Noise Level = Measured Noise Level - Baseline Level (If the measured noise level is lower than the baseline level, the construction noise level will be taken as the measured one)

Title
Route 8 (previously known as Route 9) between Cheung Sha Wan & Sha Tin
Contract HY/2003/02 - Eagle's Nest Tunnel and Associated Works

Graphical Presentation of Construction Noise Monitoring Results

CONSU	uction noise	e ieve	i wili be takei
Scale		Projec	ct
	N.T.S	No.	MA3024
Date		Apper	ndix
	Nov 07		G



APPENDIX H SUMMARY OF EXCEEDANCE

Summary of Exceedances Recorded in the Reporting Month

- a) Exceedance Report for 1-hr TSP: (NIL)
 - No Action/Limit Level exceedance was recorded in the reporting month.
- b) Exceedance Report for 24-hr TSP: (NIL)
 - No Action/Limit Level exceedance was recorded in the reporting month.
- c) Exceedance Report for Construction Noise: (NIL)
 - No Action/Limit Level exceedance was recorded in the reporting month.

APPENDIX I SITE AUDIT SUMMARY

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	71107-ENT
Date	7 November 2007 (Wed)
Time	14:20 – 15:40

Ref. No.	Non-Compliance	Related Item No.
<u> </u>	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	A. Water Quality	
	No environmental deficiency was identified during the site inspection.	
	B. Air Quality	
	No environmental deficiency was identified during the site inspection.	
	C. Noise	
	No environmental deficiency was identified during the site inspection.	
	D. Waste / Chemical Management	
•	No environmental deficiency was identified during the site inspection.	
	E. Permit / Licenses	
	No environmental deficiency was identified during the site inspection.	
	F. Others	
	• Follow-up on previous audit (Ref. No.: 71031C-ENT), all environmental	
	deficiency were rectified by the Contractor.	}
	• Covering of loaded truck leaving the site was checked during the site	
	inspection. No uncovered truck leaving the construction site was	
	observed during the site inspection.	

	Name	Signature	Date
Recorded by	Grace Wong	Orace-	7 November 2007
Checked by	Dr. Priscilla Choy	WI	7 November 2007

CINOTECH MA3024 71107_ENT

Route 8 - Environmental Team for Lai Chi Kok Viaduct and Eagle's Nest Tunnel Contract No. HY/2003/05 - Traffic Control and Surveillance System

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	71107-ENT-TCSS
Date	7 November 2007 (Wednesday)
Time	14:30-14:40

Ref. No.	Non-Compliance	Related Item No
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No
	A. Water Quality	
	No environmental deficiency was identified during the site inspection.	
	B. Air Quality	
	No environmental deficiency was identified during the site inspection.	
	C. Noise	
	No environmental deficiency was identified during the site inspection.	
	D. Waste / Chemical Management	
	No environmental deficiency was identified during the site inspection.	
	E. Permit / Licenses	
	No environmental deficiency was identified during the site inspection.	
	F. Others	
	• Follow-up for previous audit session (Ref. No.: 71009-ENT-TCSS), no	
	environmental deficiency was identified during the site inspection.	

	Name	Signature	Date
Recorded by	Grace Wong	Grace	7 November 2007
Checked by	Dr. Priscilla Choy	WIL	7 November 2007

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	71114-ENT
Date	14 November 2007 (Wed)
Time	09:20 – 11:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	A. Water Quality	
	No environmental deficiency was identified during the site inspection.	
	B. Air Quality	
	No environmental deficiency was identified during the site inspection.	
	C. Noise	
	• No environmental deficiency was identified during the site inspection.	
	D. Waste / Chemical Management	
	No environmental deficiency was identified during the site inspection.	
	E. Permit / Licenses	
	No environmental deficiency was identified during the site inspection.	
	F. Others	
	• Follow-up on previous audit (Ref. No.: 71107C-ENT), no environmental	
	deficiency was observed.	
	Covering of loaded truck leaving the site was checked during the site	
	inspection. No uncovered truck leaving the construction site was	
	observed during the site inspection.	

	Name	Signature	Date
Recorded by	Robert Tsang	Trica	14 November 2007
Checked by	Dr. Priscilla Choy	WIL	14 November 2007

CINOTECH MA3024 71114_ENT

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	71121-ENT
Date	21 November 2007 (Wed)
Time	09:40 – 11:00

 Ref. No.	Non-Compliance	Related Item No.
-	None identified	

Ref. No.	Remarks/Observations	Related Item No.
	A. Water Quality	
	No environmental deficiency was identified during the site inspection.	
	B. Air Quality	
	No environmental deficiency was identified during the site inspection.	
	C. Noise	
	No environmental deficiency was identified during the site inspection.	
	D. Waste / Chemical Management	
	• No environmental deficiency was identified during the site inspection.	
	E. Permit / Licenses	
	No environmental deficiency was identified during the site inspection.	
	F. Others	
	• Follow-up on previous audit (Ref. No.: 71114C-ENT), no environmental	
	deficiency was observed.	j
	• Covering of loaded truck leaving the site was checked during the site	
	inspection. No uncovered truck leaving the construction site was	
	observed during the site inspection.	

	Name	Signature	Date
Recorded by	Grace Wong	Grace.	21 November 2007
Checked by	Dr. Priscilla Choy	WIT	21 November 2007

CINOTECH MA3024 71121_ENT

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	71128C-ENT
Date	28 November 2007 (Wed)
Time	09:30 – 11:15

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	A. Water Quality	
	No environmental deficiency was identified during the site inspection.	
	B. Air Quality	
	No environmental deficiency was identified during the site inspection.	<u> </u>
	C. Noise	
	No environmental deficiency was identified during the site inspection.	
	D. Waste / Chemical Management	
	No environmental deficiency was identified during the site inspection.	
	E. Permit / Licenses	
	No environmental deficiency was identified during the site inspection.	
	F. Others	
	• Follow-up on previous audit (Ref. No.: 71121C-ENT), no environmental	
	deficiency was observed.	
	• Covering of loaded truck leaving the site was checked during the site	
	inspection. No uncovered truck leaving the construction site was	
	observed without cover during the site inspection.	

	Name	Signature	Date
Recorded by	Grace Wong	Grace.	28 November 2007
Checked by	Dr. Priscilla Choy	WI	28 November 2007

CINOTECH MA3024 71128_ENT

APPENDIX J EVENT ACTION PLANS

Appendix J - Event Action Plans

Event/Action Plan for Air Quality

EVENT		ACTIO	N	
EVENI	ET	IEC	ER	Contractor
ACTION LEVEL				
1. Exceedance for one	1. Identify source	1. Check monitoring data submitted by ET	1. Notify Contractor	1. Rectify any unacceptable practice
sample	2. Inform ER & IEC	2. Check Contractor's working methods	2. Check monitoring data and Contractor's	2. Amend working methods if
	3. Repeat measurement to confirm finding		working methods	appropriate
	4. Increase monitoring frequency to daily			
2. Exceedance for two or	1. Identify source	1. Checking monitoring data submitted by	1. Confirm receipt of notification of failure	1. Submit proposals for remedial
more consecutive samples	2. Inform ER & IEC	ET	in writing	actions to ER within 3 working days
	3. Repeat measurement to confirm findings	2. Check Contractor's working methods	2. Notify Contractor	of notification
	4. Increase monitoring frequency to daily	3. Discuss with ET and Contractor on	3. Check Contractor's working methods	2. Implement the agreed proposals
	5. Discuss with ER & for remedial actions	possible remedial measure	4. Discuss with ET, IEC and Contractor on	3. Amend proposal if appropriate
	required	4. Advise the ER & ET on the effectiveness	proposed remedial actions	
	6. If exceedance continues, arrange	of the proposed remedial measures	5. Ensure remedial actions properly	
	meeting with ER & IEC	5. Supervise the implementation of the	implemented	
	7. If exceedance stops, cease additional	remedial measures		
	monitoring			
LIMIT LEVEL				
1. Exceedance for one	1. Identify source	Checking monitoring data submitted by	1. Confirm receipt of notification of failure	1. Take immediate action to avoid
sample	2. Inform ER & IEC and EPD	ET	in writing	further exceedance
	3. Repeat measurement to confirm finding	2. Check Contractor's working methods	2. Notify Contractor	2. Submit proposals for remedial
	4. Increase monitoring frequency to daily	3. Discuss with ET and Contractor on	3. Check Contractor's working methods	actions to ER within 3 working days
	5. Assess effectiveness of Contractor's	possible remedial measure	4. Discuss with ET, IEC and Contractor on	of notification

EVENT		ACTIO:	N	
EVENT	ET	IEC	ER	Contractor
	remedial actions and keep EPD and ER &	4. Advise the ER & ET on the effectiveness	proposed remedial actions	3. Implement the agreed proposals
	IEC informed of the results	of the proposed remedial measures	5. Ensure remedial actions properly	4. Amend proposal if appropriate
		5. Supervise the implementation of the	implemented	
		remedial measures		
2. Exceedance for two or	1. Identify source	1. Checking monitoring data submitted by	1. Confirm receipt of notification of failure	1. Take immediate action to avoid
more consecutive samples	2. Inform ER, IEC, Contractor and EPD	ET	in writing	further exceedance
	the cause & actions taken for the	2. Discuss amongst ER, ET and Contractor	2. Notify Contractor	2. Submit proposals for remedial
	exceedances	on possible remedial measures	3. Carry out analysis of Contractor's	actions to IEC, ER within 3 working
	3. Repeat measurement to confirm findings	3. Review Contractor's remedial measures	working procedures to determine possible	days of notification
	4. Increase monitoring frequency to daily	whenever necessary to ensure their	mitigation to be implemented	3. Implement the agreed proposals
	5. Investigate the causes of exceedance	effectiveness and advise the ER	4. Discuss amongst ET, IEC and the	4. Resubmit proposals if problem
	6. Carry out analysis of contractor's	accordingly	Contractor on proposed remedial actions	still not under control
	working procedures to determine possible	4. Supervise the implementation of the	5. In consultation with IEC, agree with the	5. Stop the relevant portion of works
	mitigation to be implemented.	remedial measures	contractor remedial measures to be	as determined by the ER until the
	7. Arrange meeting with EPD, IEC and ER		implemented	exceedance is abated
	to discuss the remedial actions to be taken		6. Ensure remedial measure are properly	
	8. Assess effectiveness of Contractor's		implemented	
	remedial actions and keep EPD and ER &		7. If exceedance continues, consider what	
	IEC informed of the results		portion of the work is responsible and	
	9. If exceedance stops, cease additional		instruct the Contractor to stop that portion	
	monitoring		of work until the exceedance is abated	

Event/Action Plan for Construction Noise

Exceedance		ACTIO	N	
Exceedance	ET	.IEC	ER	Contractor
Action Level	1. Discuss with the IEC and ER and seek to	1. Review the analyzed results submitted	1. Confirm receipt of notification of	1. Submit proposals for remedial
	identify potential noise source	by the ET	complaint and notify Contractor	actions to ER within three working
			immediately	days of notification
	2. Undertake noise measurement to	2. Review the proposed remedial measures	2. Check monitoring data trends and	2. Amend proposals if required by
	confirm the validity of complaint	by the Contractor and advise the ER & ET	Contractor's working methods	the Engineer
		accordingly		
	3. Inform ER&IEC in writing	3. Supervise the implementation of	3. Remind the Contractor of his contractual	3. Implement the remedial actions
	Discuss remedial actions required with	remedial measures	obligations and discuss with ET, IEC and	immediately upon instruction
	ER&IEC if an exceedance is recorded		Contractor on proposed remedial actions	
	4. Increase monitoring frequency to		4. Assess the efficacy of remedial actions	4. Liaise with the ER to optimize the
	demonstrate efficacy of remedial measures		and keep the Contractor informed	effectiveness of the agreed
				mitigation
	5. If exceedance continues, meet with		5. Inform complainant of actions taken	5. Amend proposal if appropriate
	ER&IEC to review implementation of			
	appropriate mitigation measures.			
	6. If exceedance stops, cease additional			
	monitoring			

Exceedance		ACTIO	N	
Exceedance	ET	IEC	ER	Contractor
Limit Level	1. Repeat measurement to confirm findings	1. Check monitoring data submitted by ET	1. Confirm receipt of notification of	1. Take immediate action to avoid
			exceedance and notify Contractor	further exceedance
	2. Investigate the cause of the exceedance	2. Review Contractor's remedial actions to	2. Check monitoring data trends and	2. Submit proposals for remedial
	and identify the main source(s) of impact	assure their effectiveness and advise the	Contractor's working methods	actions to ER immediately not more
		ER &ET accordingly		than 3 working days of notification
	3. Inform ER&IEC and EPD in writing	3. Supervise the implementation of the	3. Discuss with ET, IEC and Contractor on	3. Amend proposals if required by
		remedial measures	proposed remedial actions to be	the ER
			implemented	
	4. Discuss remedial actions required with		4. Assess the efficacy of remedial actions	4. Implement remedial actions
	ER&IEC		and keep the Contractor informed	immediately upon instruction
	5. Increase monitoring frequency to		5. If exceedance continuous, consider what	5. Liaise with the ER to optimize the
	demonstrate efficacy of remedial measures		portion of the work is responsible and	effectiveness of the agreed
			instruct the Contractor to stop that portion	mitigation
			of work until the exceedance is aborted	
	6. Assess efficacy of remedial actions and			6. Resubmit proposals if problem
	keep ER & IEC informed of the results			still not under control
	7. If exceedance continues, meet with			7. Stop the relevant portion of works
	ER&IEC to identify appropriate mitigation			as determined by the ER until the
	measures			exceedance is aborted
	8. If exceedance stops, cease additional			
	monitoring			

APPENDIX K ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE (EMIS)

Appendix K - Summary of Environmental Mitigation Implementation Schedule

Types of Impacts	Mitigation Measures	Status
-	 Any stockpile of dusty materials or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water so as to maintain the entire surface wet. 	^
	 A stockpile of dusty materials should not extend beyond the pedestrian barriers, fencing or traffic cones. 	٨
	 Vehicle washing facilities should be provided at every exit point. 	^
	• The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.	^
	• Where a site boundary adjoins a road, street, service lane or other area accessible to the public, hoarding of not less than 2.4m high from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit.	۸
Construction Dust	• Every main haul road should be sprayed with water or a dust suppression chemical so as to maintain the entire road surface wet.	^
Dust	• The portion of any road leading only to a construction site that is within 30m of a discernible or designated vehicle entrance or exit should be kept clear of dusty materials.	^
	• Any stockpile of dusty materials should be either covered entirely be impervious sheeting, placed in an area sheltered on the top and the 3 sides or sprayed with water or a dust suppression chemical so as to maintain the entire surface wet.	۸
	 All dusty materials should be sprayed with water or a dust suppression chemical immediately prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet. 	^
	 Every vehicle should be washed to remove any dusty materials from its body and wheels immediately before leaving a construction site. 	۸
	• The working area of any excavation should be sprayed with water or a dust suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet.	۸
Construction Noise	 Only well-maintained plant should be operated on –site and plant should be serviced regularly during the construction works. 	٨
	 Machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum. 	^
	 Plant know to emit noise strongly in one direction, should where possible, be orientated to direct noise away from the NSRS. 	^
	 Mobile plant should be sited as far away from NSRs as possible. 	^
	 Material stockpiles and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities. 	^
	Use quite plant and Working Method	^
	 Reduce the number of plant operating in critical areas close NSRs. 	٨

Types of Impacts	Mitigation Measures	Status
	Construct temporary and movable noise barriers	٨
Water Quality	Construction Runoff and Drainage	
	Use of sediment traps and the adequate maintenance of drainage systems to prevent flooding and overflow.	٨
	 Boundaries of critical areas of earthworks should be marked and surrounded by dykes or embankments for flood protection. Temporary ditches should be provided to facilities runoff discharge into the appropriate watercourses, via a silt retention pond. Permanent drainage channels should incorporate sediment basins or traps and baffles to enhance deposition rates. 	٨
	 All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment traps should be regularly cleaned and maintained. The temporarily diverted drainage should be reinstated to its original condition when the construction works has finished or the temporary diversion is no longer required 	^
	 Sand silt in the wash water from the wheel washing facilities, which ensure no earth, mud and debris is deposited on roads, should be settled out the removed before discharging into storm drains. A section of the road between the wheel washing bay and the public road should be paved with backfill to prevent wash water or other site runoff form entering public road drains. 	^
	 Oil interceptors should be provided in the drainage system and regularly emptied to prevent the release of oils and grease into the storm water drainage system after accidental spillage. The interceptor should have a bypass to prevent flushing during periods of heavy rain. 	٨
	 Catchpits and perimeter channels shall be constructed in advance of site formation works and earthworks. 	^
	• Silt removal facilities, channels and manholes shall be suitably maintained with the deposited silt and grit being removed at least once a week, and at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times.	^
	• Earthworks final surfaces shall be well compacted and the subsequent permanent work or surface protection shall be carried out immediately after the final surfaces are formed to prevent erosion caused by rainstorms. Appropriate intercepting channels shall be provided along the site boundary or at the locations agreed with the ET Leader. Rainwater pumped out from trenches or foundation excavations shall be discharged into silt removal facilities before discharge into storm drains.	^
	 All generators, fuel and oil storage shall be within bunded areas. Drainage from the areas shall be connected to storm drains via a petrol interceptor. 	٨
	Tunnelling Work	
	 Temporary open storage of excavated materials should be covered with tarpaulin or similar fabric during rainstorms. Any washout of construction or excavated materials form the drill and blast tunnelling work should be diverted to the drainage system via appropriate sediment traps. 	٨
	 Ground water pumped out of tunnels should be discharged into the drainage channels which incorporated sediment traps to enhance deposition rates and to remove silt. 	٨

Types of Impacts	Mitigation Measures	Status
-	 Spend grouts used in diaphragm wall construction should be collected in a separate slurry collection system, reconditioned and reused wherever practicable. The disposal of used grouting materials will only be permitted if it is treated to the TM standards before discharge to the storm drains or disposal to landfill. 	N/A
	General Construction Activities	
	 Debris and rubbish on site should be collected, handled and disposed of properly to avoid entering the water column and cause water quality impacts. 	^
	• All fuel tanks and storage areas will be provided with locks and be located on sealed areas (within bunds of a capacity equal to 110% of the storage capacity of the largest tank or 20% by volume of the fuel stored in that areas, whichever in the greatest).	^
	Sewage Effluent	
	 Construction work force sewage discharges form fixed toilet facilities on-site should be connected to the nearby existing trunk sewer wherever feasible. However, for areas where existing trunk sewer is not available, it is recommended that appropriate and adequate on site portable chemical toilets should be provided by a licensed contractor who will be responsible for appropriate disposal and maintenance of these facilities. 	^
	• It is considered that sewage discharges could also be treated by on-site septic tanks and soakaway. Minimum clearance away form streams and catchments and other requirements for the proposed septic tank and soakaway should be referred to EPD's Practice Note for Professional Persons, Drainage Plans.	N/A
Waste	General	
	 Training and instruction shall be given at a site to construction staff to increase awareness and draw attention to waste management issues and the need to minimise waste generation. The training requirement shall be included in the site waste management plan. 	^
	Storage, Collection and Transportation of Waste	
	 Wastes shall be handled and stored in a manner to ensure that they are held securely without loss or leakage. 	^
	 Authorised or licensed waste hauliers shall be used and they shall only collect wastes prescribed by their permits. 	^
	Waste shall be removed on a daily basis.	^
	 Waste storage area shall be maintained and cleaned on a daily basis. 	^
	 Windblown litter and dust during transportation shall be minimised by either covering trucks or transporting wastes in enclosed containers. 	^
	 Obtain necessary waste disposal permits from the appropriate authorities if they are required. 	^
	 Wastes shall be disposed of at licensed waste disposal facilities. 	^
	 Develop procedure such as ticketing system to facilitate tracking of loads, particularly for chemical waste, and to ensure that illegal disposal of wastes does not occur. 	٨
	 Maintain records of the quantities of wastes generated, recycled and disposed. 	^

Surplus Excavated Materials	
• Due to the high risk of loose material being washed into the existing nullah, stockpile materials should be properly compacted and covered from water erosion and located at least 10m away from the nullah wall.	^
Construction and Demolition (C&D) Waste	
 Careful design, planning and good site management shall be adopted to minimise over-ordering and generation of waste materials such as concrete grouts. 	^
• The handling and disposal of bentonite slurries shall be undertaken in accordance with Practice Note for Professional Persons – Construction Site Drainage (ProPECC PN 1/94) on construction site drainage.	N/A
• Construction and demolition (C&D) material shall be segregated to inert and non-inert parts. The inert portion shall re-used at areas of reclamation or land formation, or to public filling area shall such allocation is deemed necessary. The non-inert portion shall be disposed of to landfill.	^
Chemical Waste	
• Chemical waste that is produce during construction shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes.	^
 Containers used for the storage of chemical wastes should: a. Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; b. Have a capacity of less than 450 litres unless the specifications have been approved by the EPD; c. Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Chemical Waste Regulations 	٨
 The storage area for chemical wastes should: a. Be clearly labelled and used solely for the storage of chemical waste; 	
 c. Have an impermeable floor and bunding of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is largest; d. Have adequate ventilation; 	^
e. Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste if necessary);f. Be arranged so that incompatible materials are adequately separated.	
 Disposal of chemical waste shall be via a licensed waste collector; and to a facility licensed to receive chemical waste; or a reuser of the waste (under approval from EPD). 	^
	 Construction and Demolition (C&D) Waste Careful design, planning and good site management shall be adopted to minimise over-ordering and generation of waste materials such as concrete grouts. The handling and disposal of bentonite slurries shall be undertaken in accordance with Practice Note for Professional Persons – Construction Site Drainage (ProPECC PN 1/94) on construction site drainage. Construction and demolition (C&D) material shall be segregated to inert and non-inert parts. The inert portion shall re-used at areas of reclamation or land formation, or to public filling area shall such allocation is deemed necessary. The non-inert portion shall be disposed of to landfill. Chemical Waste Chemical waste that is produce during construction shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes. Containers used for the storage of chemical Wastes should: a. Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; b. Have a capacity of less than 450 litres unless the specifications have been approved by the EPD; c. Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Chemical Waste Regulations. The storage area for chemical wastes should: a. Be clearly labelled and used solely for the storage of chemical waste; b. Be enclosed on at least 3 sides; c. Have an impermeable floor and bunding of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is largest; d. Have adequate ventilation; e. Be covered to prevent rainfall entering (water collected with


Types of Impacts	Mitigation Measures	Status
	General Refuse	
	• General refuse generated on-site shall be stored in enclosed bins or compaction unit separate from C&D and chemical wastes. A reputable waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D and chemical wastes, on a daily for every second day basis to minimise odour, pest and litter impacts. The burning of refuse on construction sites is prohibited by law.	
	Reusable rather than disposable dishware shall be used if feasible.	٨
	A sediment barrier shall be erected to minimize stream sedimentation at downstream of the project boundary of the Toll Plaza.	N/A
	Conduct a tree survey before commencement of the construction work.	^
Ecology	• All measures recommended in the approved landscape proposals under Condition 2.4 in EP above shall be fully implemented in accordance with the details and time schedule set out in the submission.	N/A
	 Loss of the adjacent woodland due to temporary land take shall be returned to the original status immediately. Wild and uncontrolled fire shall be strictly prohibited 	N/A
	• Fences shall be erected along the boundary of the construction sites at the Toll Plaza before commencement of works, to prevent tipping, vehicle movements, and encroachment of personnel onto adjacent wooded areas.	N/A
	• Landscape mitigation measure 1 (LMM1) – Construction programming and management. The periphery of the works areas at street level shall be managed so that they do not appear cluttered, untidy and unattractive and inconvenient to pedestrians. For example, all hoarding shall be colorfully designed with interesting motifs demonstrating the work of Highways Department. Hoardings with bland colours shall be avoided.	٨
Landscape and Visual Impact	• Landscape mitigation measure 2 (LMM2) – Advanced planting and erosion control works. Where possible, the transplantation of existing valuable trees, the stockpiling of topsoil, new planting and erosion control works shall be carried out as early as possible in the construction period instead of at the end. This will assist in maximizing the time for carrying out transplantation and new planting, resulting in a higher success rate for the survival of transplantation and new planting, resulting in a higher success rate for the survival of transplanted trees and the establishment of new screen trees. The stockpiling of topsoil will provide an abundant use of on-site material for growing media. During detailed design, the issue of stockpiling of topsoil in a manner that would avoid washing into the drainage scheme should be examined comprehensively.	۸
	 Measurement of vibration would also be carried out on a need basis during the piling work 	٨

Compliance of mitigation measure; Not Applicable; Remarks: ٨ N/A

X


Non-compliance of mitigation measure; Non-compliance but rectified by the contractor


APPENDIX L CONSTRUCTION PROGRAMME

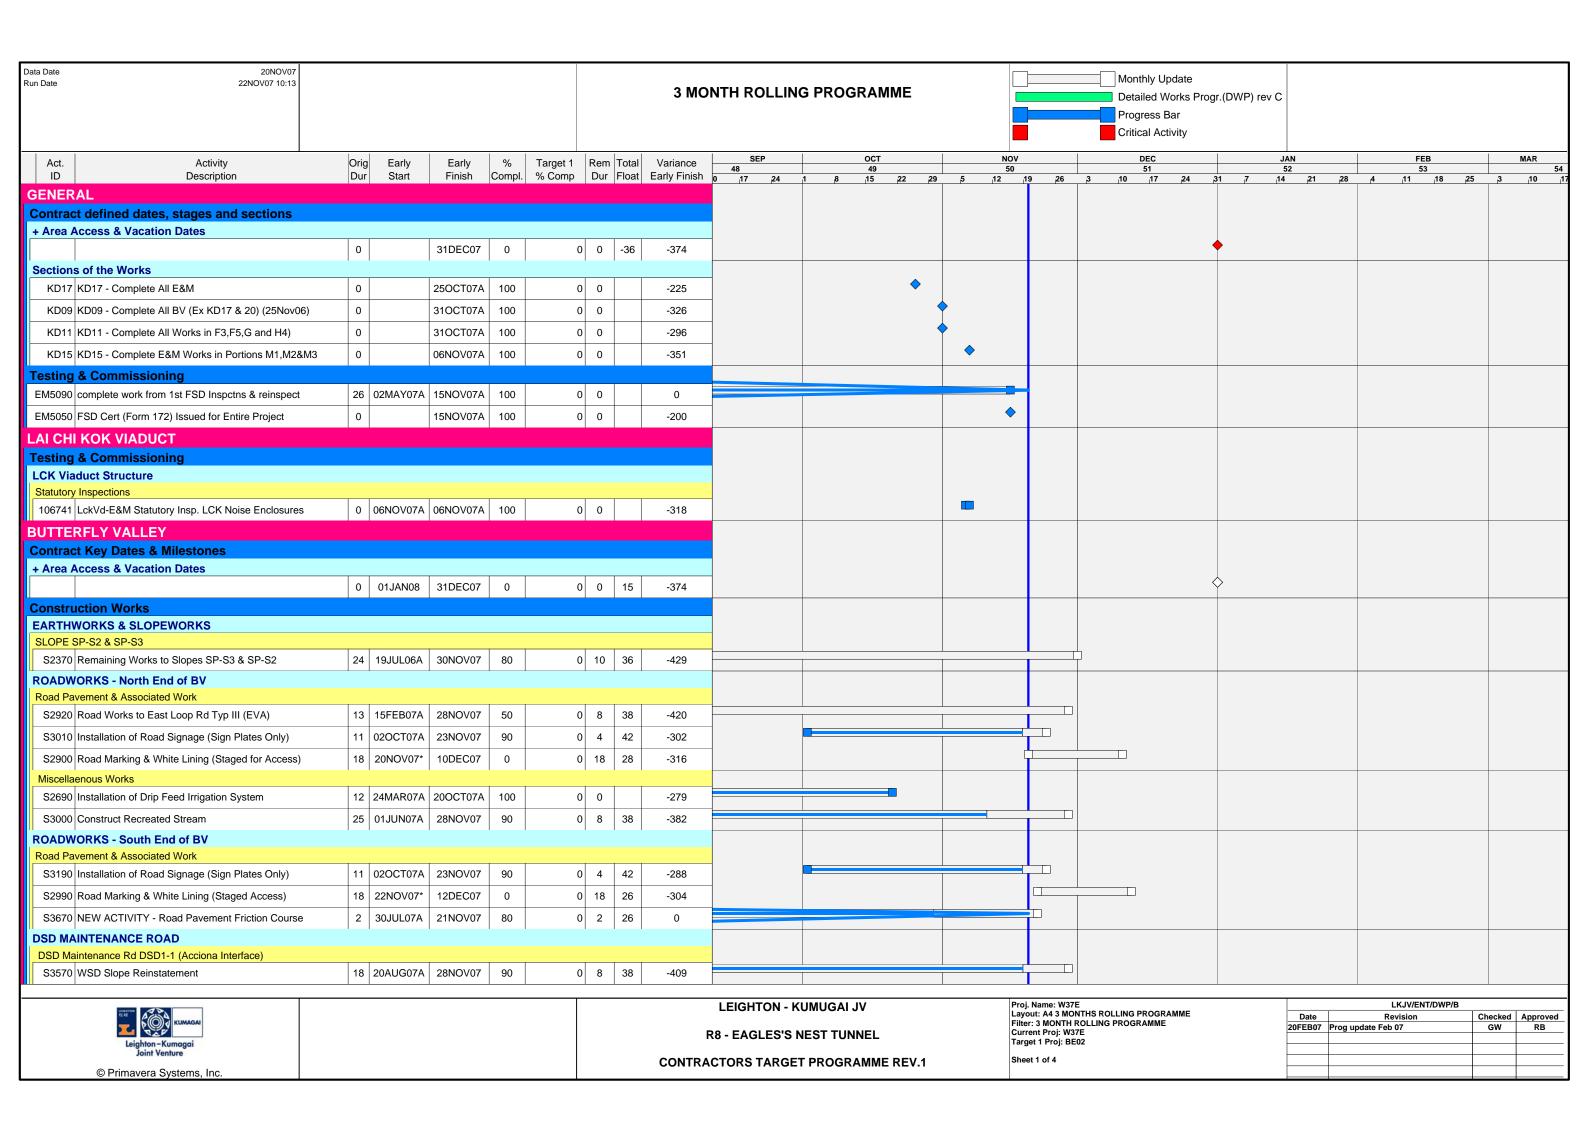


Act. Activity ID Description	Orig Early Dur Start	Early Finish (Target 1 Ren % Comp Dui	n Tota		SEP OCT 48 49	NOV 50		DEC 51	JAN 52	FEB 53
Description Description Description Description	Dur Start	rinish (Compi.	% Comp Dui	Floa	t Early Finish	0 ,17 ,24 ,1 ,8 ,15 ,22 ,29	5 12	19 26	3 10 17 24 31	,7 ,14 ,21 ,28	<u>4</u> 11 18 25 3
22730 Construct Recreated Stream	45 27MAR07A 1	16NOV07A	100	0 0		-306						
S2700 Access rd DSD1 -barrier footings		26NOV07	90	0 6	40	-412						
S2720 Access rd DSD1 - Barriers		26NOV07	90	0 6								
									\Diamond			
S3160 REINSTATE BV ACCESS	0	26NOV07	0	0 0	40	-315			<u> </u>			
andscaping & Establishment												
101476 BV - Soft Landscaping & Planting		26NOV07	94	0 6								
101475 BV - Hard Landscaping	90 03JAN07A	26NOV07	90	0 6	-256	-347			_			
101477 BV - Establishment works	365 27NOV07	25NOV08	0	0 365	-315	-220						
NT SOUTH PORTAL VENTILATION BUILDING												
ONSTRUCTION												
outh Portal Bldg CIVIL & ABWF WORKS												
BWF WORKS												
Roof & External Facade T2360 Ent SPB - GMS,S/S Roof Balustrade & Railing	24 24MAR07A	30NOV07	70	0 10	36	-341						
T2390 Ent SPB - Expanded metal cladding to Ext Walls	18 08SEP07A	Z8NOVU/	60	0 8	38	-348						
NT South Portal Bldg BUILDING SERVICES												
Eatly WORKS Statutory Inspection & Issued Certificates												
M1340 Water Supply Certificate issued	0 0	01NOV07A	100	0 0		-373		>				
AGLES NEST TUNNEL												
ontract defined dates, stages & sections												
Area access & vacation dates												
	0 01JAN08	31DEC07	0	0 0	15	-374				\		
onstruction Works												
unnel Drive North Bound												
NT NB TUNNEL - (E&M) BUILDING SERVICES												
Clectrical Works Below OHVD	60 40MADOZA 6	200CT074	100	0 0		204						
278013 Ent NB - Lighting / Equipt Testing and T&C	60 19MAR07A 2	200010/A	100	0 0		-304						
unnel Drive South Bound unnel Finishing Works												
Bituminous Pavement												
1340 SB Road Marking	14 13OCT07A 1	15NOV07A	100	0 0		-231						
NT SB TUNNEL - (E&M) BUILDING SERVICES												
Electrical Works Below OHVD												
278056 Ent SB - Lighting / Equipt Testing and T&C	60 15JAN07A 2	20OCT07A	100	0 0		-280						
ENTILATION ADIT & BUILDING												
ONSTRUCTION WORKS												
XTERNAL WORKS												
Orainage S1970 Storm Drain & Gullies at Access Apron	24 14APR07A	28/10//07	90	0 8	20	-404						
	Z4 I4APKU/A	20INUVU/	90	υ 8	38	-404						
Oucting & Drawpits S1980 HGC Ducting & Drawpits	18 16APR07A 1	15NOV074	100	0 0		222						
	10 TOAPROTA I	ISINOVUIA	100	0 0		-333						
Road Pavement & Associated Work S1920 Preparation and Block Paving	22 13JUN07A	19NOV07	85	0 0	34	-288			_			
S1930 Signage, furniture and finishes	24 20JUL07A	U3DEC07	65	0 11	34	-276						
ENTILATION BUILDING												
A Building - ABWF A Building - External Finishes												
A Dallaing External Filliones		4005007	05	2 42		070			_			
T2110 VA Bldg Expanded metal cladding to Ext Walls	18 20OCT07A	10DEC07	65	0 18	28	-372						

A at	A sakin ika n	Orio Forty	Forb.	0/	Torrect 1 D	Total	al Variance	SEP	ост	NOV		DEC	JAN	FEB MAR
Act.	Activity Description	Orig Early Dur Start	Early Finish	% Compl.		Rem Tota Our Floa	al Variance at Early Finish	48 0 17 24 1	49 8 15 22 29	50	19 26	51	52 1 7 14 21 28	53
E&M V														
	nspection & Issued Certificates		04NOV07A	100	0	0	-247							
	Water Supply Certificate issued	0	01NOV07A	100	0	0	-247							
	IAL AREAS CAPING & ESTABLISHMENT WORKS													
	Planting Works	18 02SEP06A	26NOV07	95	0	6 -29	6 -342							
			_					_						
	Establishment Works	365 27NOV07	25NOV08	0	0 3	365 -36	6 -423							
	ORTH PORTAL VENTILATION BUILDING													
	RUCTION													
	Portal Bidg CIVIL & ABWF WORKS													
<mark>ABWF W</mark> NP Bldg - I	Roofing & External Facade													
	Ent NPB - GMS,S/S Channel, Balustrade & Railing	24 05MAR07/	4 28NOV07	85	0	8 38	-377							
T1780	Ent NPB - Slate replacement cladding above NB/SB	36 09JUL07A	13NOV07A	100	0	0	-361							
	Ent NPB - Expanded metal cladding to Ext Walls	18 12SEP07A		75	0 .									
		10 12321077	03DEC07	73	٥	12 34	-332							
	LAZA & ANCILLIARY STRUCTURES													
	ACCESS * VACATION DATES													
AKEA	ACCESS & VACATION DATES	0 04 14 100	2105007	0	0	0 45	274					<	>	
		0 01JAN08	31DEC07	0	0	0 15	-374							
	Iction Works													
	LAZA EAST SIDE	EG 4000T00	12000074	100	2	0	245							
	Road Pavement Surfacing (Flex & Rigid)	56 18OCT06A			0		-315							
	East Loop Road - Formation & Roadworks	36 12JAN07A		100	0	0	-290							
S1140	Furniture, signage (face only), white lining	18 06OCT07	29NOV07	75	0	9 37	-311							
OLL PI	LAZA WEST SIDE													
K1171	West Loop road - Roadworks	36 12MAR07	13NOV07A	100	0	0	-381							
S1410	Furniture, signage (face only), white lining	18 06OCT07/	29NOV07	75	0	9 37	-278							
TOLL PI	LAZA - works adjacent to building		· ·				·							
	SHT SPB - Kerbs & Rwks & misc finishes	12 06MAR07/	A 13NOV07A	100	0	0	-434							
OLL PI	LAZA FOOTBRIDGE		1			ļ								
ABWF														
S1250	Toll Ftbrdge - Finishes	54 18JUN07A	23NOV07	95	0	4 42	-335							
ANDS	CAPING & ESTABLISHMENT WORKS		'	, ,										
S1480	Planting Works at Toll Plaza	24 10APR07	26NOV07	50	0	6 -25	6 -197							
S1490	Establishment Works at Toll Plaza	365 27NOV07	25NOV08	0	0 3	365 -31	5 -243							
	ISTRATION BUILDING													
	RUCTION													
	ABWF WORKS													
BWF														
	g (G/F) - Internal Work @ Grid 1 to 21													
	AB G/F (Grid 1-21) - Door Leaf & Final Paints	12 02JAN07A	26NOV07	90	0	6 40	-364							
	g (1/F) - Internal Work @ Grid 1 to 18	12 02JAN07A	1600/074	100		0	-345							
	AB 1/F (Grid 1-18) - Door Leaf & Final Paints				0									
	AB 1/F (Grid 1-18) - Floor Carpets	12 08OCT07/	A 17NOV07A	100	0	0	-358							
	g (2/F) - Internal Work @ Grid 1 to 18	40 40 10 10 70	16NOV074	100	2	0	244							
	AB 2/F (Grid 1-18) - Door Leaf & Final Paints	12 10JAN07A			0		-311							
TOOOO	AB 2/F (Grid 1-18) - Floor Carpets	12 08OCT07/	17NOV07A	100	0	0	-336							
12068		1 1	1	1 400		_	-324							
	AB 2/F (Corridor & Cont Rm) - Floor Carpets	12 08OCT07	17NOV07A	100	0	0	-324							
T3068	g - Upper Roof & External Facade													
T3068 Admin Bld T2340		30 03APR06A 45 15OCT06A	A 26NOV07	99	30	6 40	-446							

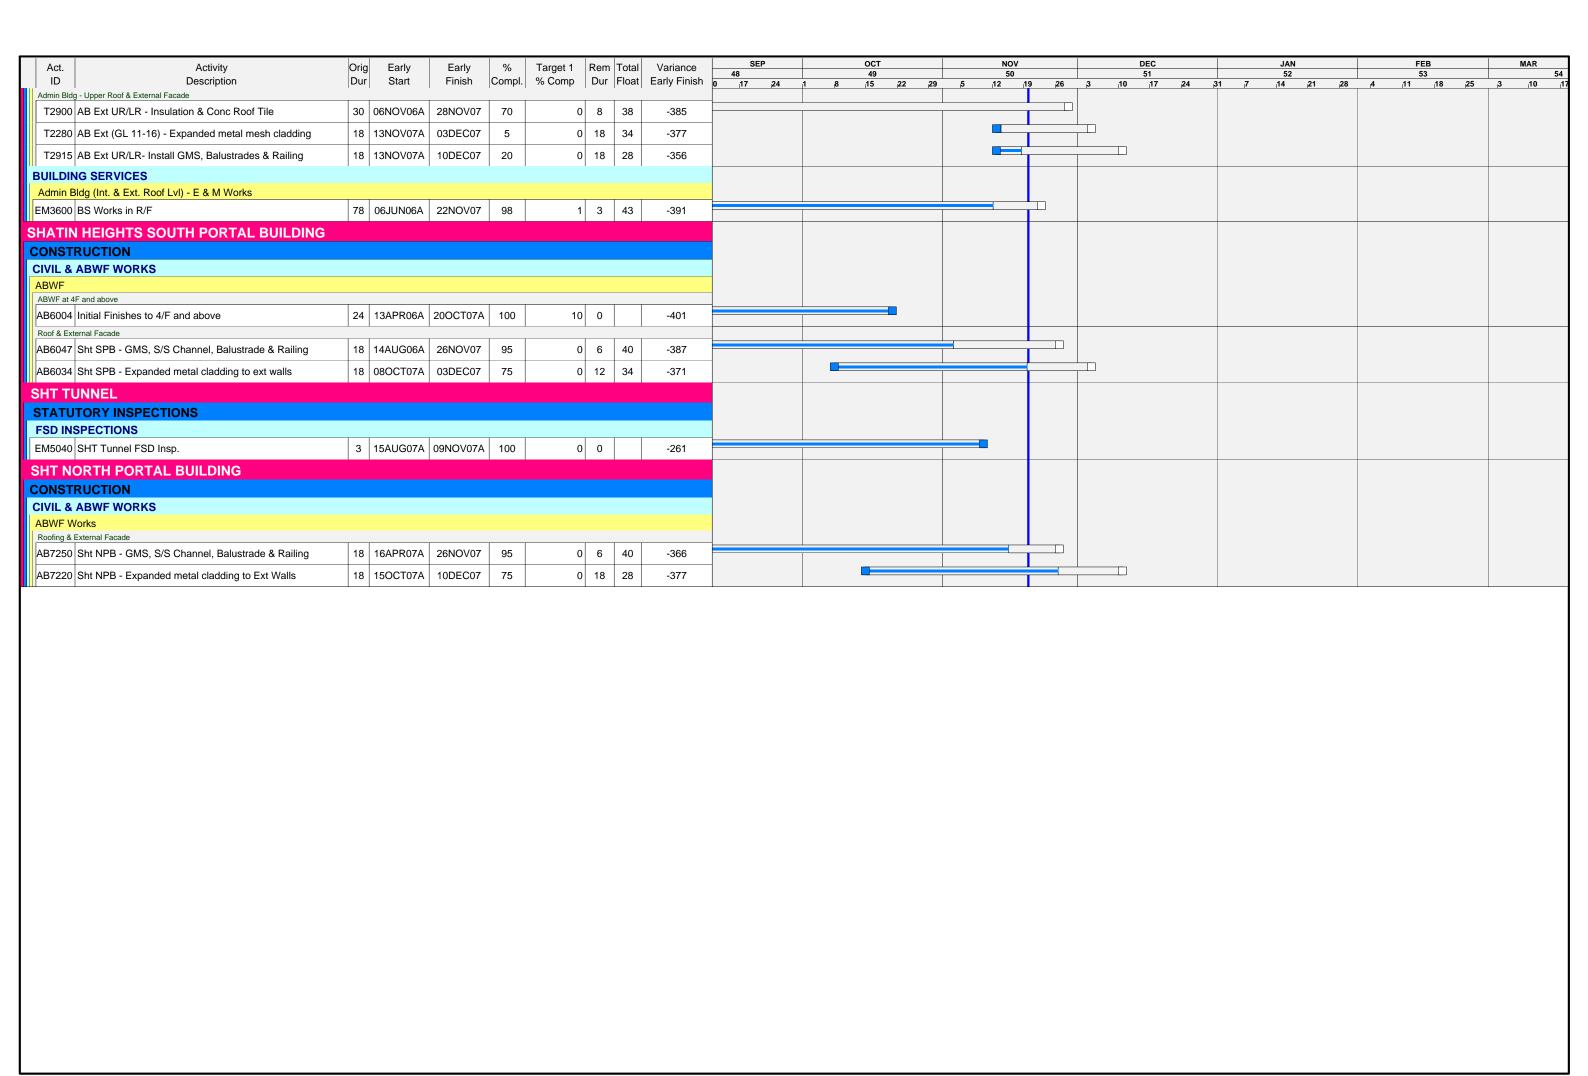

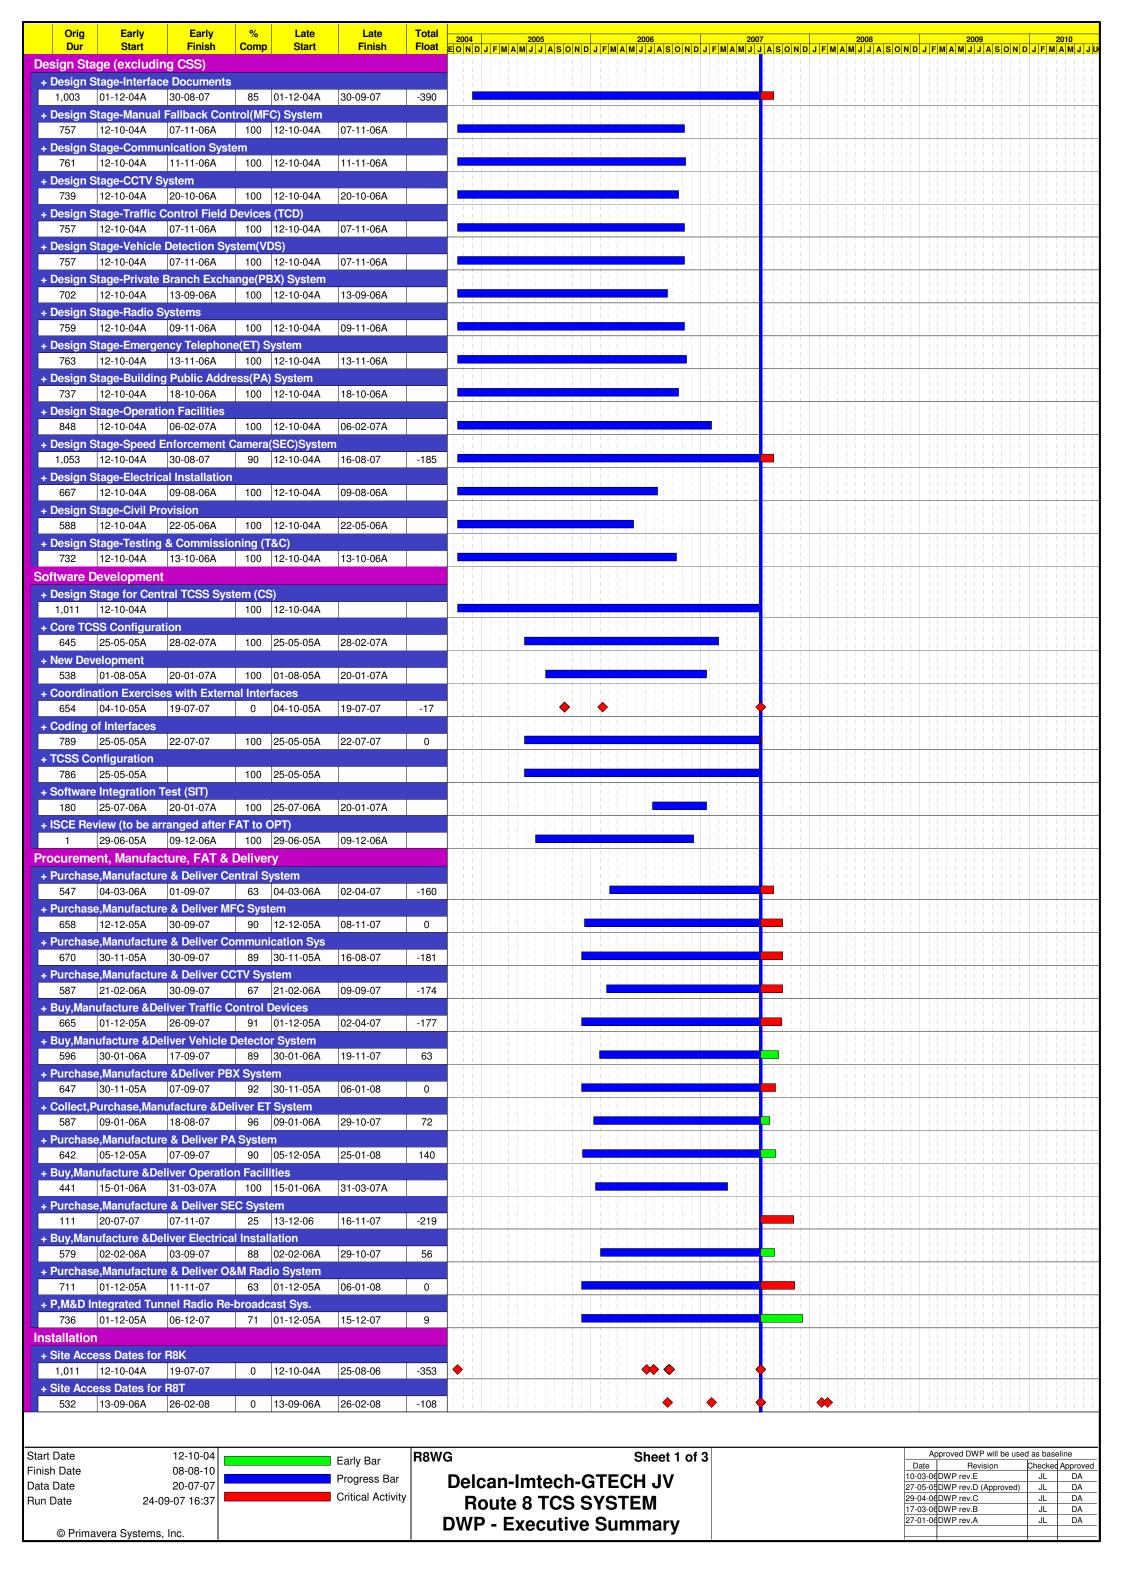

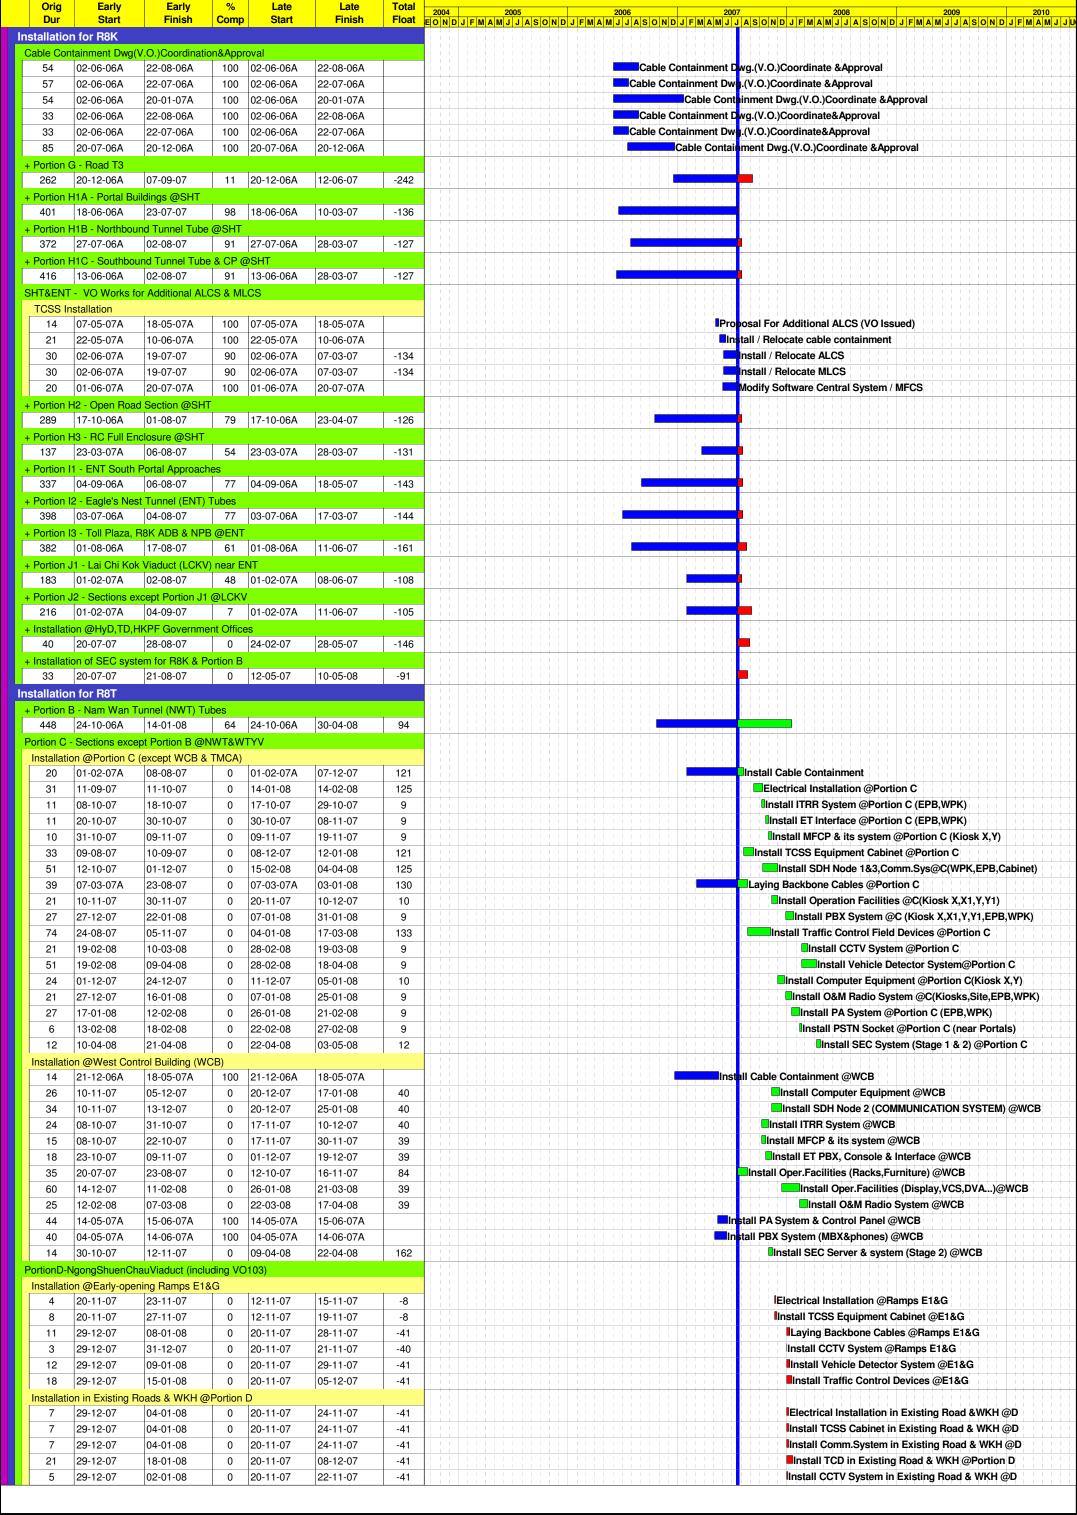

Site Commissioning Tests (SCT) @R8X 139 10-04-07A 28-08-07 7 10-04-07A 12-06-07 -228 12 09-08-07 20-08-07 0 13-05-07 10-05-08 -90 Site Commissioning Tests @R8T 12 09-08-07 20-08-07 0 13-05-07 10-05-08 -90 Site Commissioning Tests @R8T 295 20-07-07 09-05-08 0 23-11-07 12-06-09 -43 System Acceptance Tests (SAT) @R8X 89 27-07-07 23-10-07 0 23-02-07 29-05-07 -161 System Acceptance Tests (R8 with EOT) 168 19-01-08 04-07-08 0 07-12-07 07-08-08 -43 Operability Test (OPT) @R8X 58 21-09-7 20-11-07 0 14-05-07 26-06-07 -161 SAT & OPT for SEC system @R8X 58 21-09-7 20-11-07 0 24-05-07 20-09-08 -89 Operability Test (R8 with EOT) 44 08-06-08 21-07-08 0 08-06-08 20-09-08 0 Deparation and Maintenance Documents & Training Documentation for R8X 14 29-10-07 15-11-07 0 04-03-11 23-03-11 846 15 17-11ning for R8X 14 29-10-07 15-11-07 0 04-03-11 23-03-11 846 15 17-12nining for R8X 16 20-03-08 15-04-08 0 22-07-08 08-08-08 80	1.5	33	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	17-12-07 07-08-07 05-11-07 24-09-07 06-08-07 31-07-07 17-08-07 13-11-07 10-11-07 Viaduct (ETYV) 12-03-08 20-03-08 20-03-08 14-04-08 14-03-08 11-03-08 27-03-08 27-03-08 14-03-08 27-03-08 14-03-08 14-03-08	0 01-11-07 20 18-05-07A 0 17-11-07 0 07-11-07 50 04-04-07A 20 20-06-07A 0 18-10-07 0 24-11-07 0 28-11-07 0 17-11-07 0 08-03-08 0 19-03-08 0 08-03-08 0 03-04-08 0 03-04-08 0 11-04-08 0 11-04-08	29-11-07 24-11-07 23-11-07 29-11-07 30-10-07 16-11-07 01-12-07 03-12-07 24-11-07 22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	-18 109 18 66 115 90 90 18 22 18		■Install TCSS Equipment Cabinet @Portion D Laying Backbone Cables @Portion D Install Operation Facilties @Portion D (Kiosk F) Install SDH Node 4,5,6 & COMMUNICATION SYSTEM @D Install Traffic Control Field Devices @Portion D Install CCTV System @Portion D
Part Price	Part 161/25 161	29	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	17-12-07 07-08-07 05-11-07 24-09-07 06-08-07 31-07-07 17-08-07 13-11-07 10-11-07 Viaduct (ETYV) 12-03-08 20-03-08 20-03-08 14-04-08 14-03-08 11-03-08 27-03-08 27-03-08 14-03-08 27-03-08 14-03-08 14-03-08	0 01-11-07 20 18-05-07A 0 17-11-07 0 07-11-07 50 04-04-07A 20 20-06-07A 0 18-10-07 0 24-11-07 0 28-11-07 0 17-11-07 0 08-03-08 0 19-03-08 0 08-03-08 0 03-04-08 0 03-04-08 0 11-04-08 0 11-04-08	29-11-07 24-11-07 23-11-07 29-11-07 30-10-07 16-11-07 01-12-07 03-12-07 24-11-07 22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	-18 109 18 66 115 90 90 18 22 18		■Install TCSS Equipment Cabinet @Portion D Laying Backbone Cables @Portion D Install Operation Facilties @Portion D (Kiosk F) Install SDH Node 4,5,6 & COMMUNICATION SYSTEM @D Install Traffic Control Field Devices @Portion D Install CCTV System @Portion D
20 19-00	Page	24	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	07-08-07 05-11-07 24-09-07 06-08-07 31-07-07 17-08-07 13-11-07 10-11-07 Viaduct (ETYV) 12-03-08 20-03-08 20-03-08 14-04-08 14-03-08 11-03-08 27-03-08 27-03-08 27-03-08 14-03-08	20 18-05-07A 0 17-11-07 0 07-11-07 50 04-04-07A 20 20-06-07A 0 18-10-07 0 24-11-07 0 28-11-07 0 17-11-07 0 08-03-08 0 19-03-08 0 08-03-08 0 03-04-08 0 03-04-08 0 11-04-08 0 11-04-08	24-11-07 23-11-07 29-11-07 29-11-07 30-10-07 16-11-07 01-12-07 03-12-07 24-11-07 22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	109 18 66 115 90 90 18 22 18		Laying Backbone Cables @Portion D Install Operation Facilties @Portion D (Kiosk F) Install SDH Node 4,5,6 & COMMUNICATION SYSTEM @D Install Traffic Control Field Devices @Portion D Install CCTV System @Portion D
Second Control Seco	Sect 19-07	24	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	24-09-07 06-08-07 31-07-07 17-08-07 13-11-07 10-11-07 06-11-07 Viaduct (ETYV) 12-03-08 20-03-08 20-03-08 22-03-08 14-04-08 14-03-08 11-03-08 26-03-08 27-03-08 04-03-08 27-03-08 14-03-08	0 07-11-07 50 04-04-07A 20 20-06-07A 0 18-10-07 0 24-11-07 0 28-11-07 0 17-11-07 0 08-03-08 0 19-03-08 0 03-04-08 0 03-04-08 0 03-04-08 0 11-04-08 0 11-04-08	29-11-07 29-11-07 30-10-07 16-11-07 01-12-07 03-12-07 24-11-07 22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	66 115 90 90 18 22 18		Install SDH Node 4,5,6 & COMMUNICATION SYSTEM @D Install Traffic Control Field Devices @Portion D Install CCTV System @Portion D
Section Sect	Section Control Cont	36 04-04-07A 06-08-07 15 20-06-07A 31-07-07 15 20-06-07A 31-07-07 29 20-07-07 17-08-07 8 06-11-07 13-11-07 5 06-11-07 10-11-07 8 30-10-07 06-11-07 Portion E - East Tsing Yi Viaduct (ETY Installation @Portion E 15 27-02-08 12-03-08 23 27-02-08 20-03-08 23 27-02-08 20-03-08 23 27-02-08 20-03-08 248 27-02-08 14-04-08 17 27-02-08 14-03-08 14 27-02-08 11-03-08 29 27-02-08 26-03-08 114 27-02-08 11-03-08 29 27-02-08 26-03-08 Installation in Existing Roads @Portion F 7 21-03-08 27-03-08 10 05-03-08 14-03-08 11 10 05-03-08 14-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 11 11-02-08 28-02-08 18 11-02-08 28-02-08 18 11-02-08 29-02-08 18 11-02-08 29-02-08 18 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 01-	50 20 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	06-08-07 31-07-07 17-08-07 13-11-07 10-11-07 06-11-07 Viaduct (ETYV) 12-03-08 20-03-08 20-03-08 14-04-08 14-03-08 11-03-08 26-03-08 27-03-08 04-03-08 27-03-08 14-03-08	50 04-04-07A 20 20-06-07A 0 18-10-07 0 24-11-07 0 28-11-07 0 17-11-07 0 08-03-08 0 19-03-08 0 03-04-08 0 03-04-08 0 03-04-08 0 11-04-08 0 11-04-08	29-11-07 30-10-07 16-11-07 01-12-07 03-12-07 24-11-07 22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	115 90 90 18 22 18		Install Traffic Control Field Devices @Portion D Install CCTV System @Portion D
1	Fig. 20 20 20 20 20 20 20 2	15	200 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	31-07-07 17-08-07 13-11-07 10-11-07 06-11-07 Viaduct (ETYV) 12-03-08 20-03-08 20-03-08 22-03-08 14-04-08 14-03-08 11-03-08 26-03-08 27-03-08 04-03-08 27-03-08 14-03-08	20 20-06-07A 0 18-10-07 0 24-11-07 0 28-11-07 0 17-11-07 0 0 8-03-08 0 19-03-08 0 08-03-08 0 03-04-08 0 03-04-08 0 11-04-08 0 11-04-08 0 12-04-08	30-10-07 16-11-07 01-12-07 03-12-07 24-11-07 22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	90 90 18 22 18 10 21		Install CCTV System @Portion D
Second Control	Second Control Contr	29	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	17-08-07 13-11-07 10-11-07 06-11-07 Viaduct (ETYV) 12-03-08 20-03-08 20-03-08 22-03-08 14-04-08 11-03-08 11-03-08 26-03-08 27-03-08 04-03-08 27-03-08 14-03-08	0 18-10-07 0 24-11-07 0 28-11-07 0 17-11-07 0 17-11-07 0 08-03-08 0 19-03-08 0 08-03-08 0 03-04-08 0 03-04-08 0 11-04-08 0 11-04-08	16-11-07 01-12-07 03-12-07 24-11-07 22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	90 18 22 18 10 21		
3 St. 12 St. 13 St. 16 St.	1	8	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	13-11-07 10-11-07 06-11-07 Viaduct (ETYV) 12-03-08 20-03-08 20-03-08 22-03-08 14-04-08 14-03-08 11-03-08 26-03-08 27-03-08 04-03-08 27-03-08 14-03-08	0 24-11-07 0 28-11-07 0 17-11-07 0 17-11-07 0 08-03-08 0 19-03-08 0 08-03-08 0 03-04-08 0 03-04-08 0 11-04-08 0 11-04-08	01-12-07 03-12-07 24-11-07 22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	18 22 18 10 21		Install Vehicle Detector System @Portion D
\$ 0.14-02 0.14	\$ 9.0-607 (2-10) 0 1-10 (2-10)	5 06-11-07 10-11-07 8 30-10-07 06-11-07 Portion E - East Tsing Yi Viaduct (ETY Installation @Portion E 15 27-02-08 12-03-08 23 27-02-08 20-03-08 25 27-02-08 22-03-08 48 27-02-08 14-04-08 17 27-02-08 14-03-08 14 27-02-08 11-03-08 29 27-02-08 26-03-08 Installation in Existing Roads @Portion F 7 21-03-08 27-03-08 18 10-03-08 27-03-08 18 10-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 18 11-02-08 23-02-08 18 11-02-08 28-02-08 18 11-02-08 29-02-08 18 01-03-08 10-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 01-03-08 18-03-08 29-02-08 18 01-03-08 18-03-08 29-02	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	10-11-07 06-11-07 Viaduct (ETYV) 12-03-08 20-03-08 20-03-08 22-03-08 14-04-08 14-03-08 11-03-08 26-03-08 Roads @Portion E 27-03-08 04-03-08 27-03-08 14-03-08	0 28-11-07 0 17-11-07 0 08-03-08 0 19-03-08 0 08-03-08 0 03-04-08 0 03-04-08 0 03-04-08 0 11-04-08 0 11-04-08	03-12-07 24-11-07 22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	22 18 10 21		Install Ot M Padia Custom @Portion D/Kidal(E)
3 20 10 7 10 10 7 10 10 10	1	8 30-10-07 06-11-07	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	06-11-07 Viaduct (ETYV) 12-03-08 20-03-08 20-03-08 22-03-08 14-04-08 14-03-08 11-03-08 26-03-08 04-03-08 27-03-08 14-03-08 14-03-08	0 17-11-07 0 08-03-08 0 19-03-08 0 08-03-08 0 03-04-08 0 03-04-08 0 11-04-08 0 11-04-08 0 12-04-08	24-11-07 22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	10 21	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	
Parent Line Parent Par	Name of Land 1997 1998	Portion E - East Tsing Yi Viaduct (ETY Installation @Portion E 15 27-02-08 12-03-08 23 27-02-08 20-03-08 23 27-02-08 20-03-08 25 27-02-08 22-03-08 48 27-02-08 14-04-08 17 27-02-08 14-03-08 14 27-02-08 11-03-08 29 27-02-08 26-03-08 11-03-08 29 27-02-08 26-03-08 11-03-08 27-03-08 18 10-03-08 27-03-08 18 10-03-08 27-03-08 14-03-08 4 15-03-08 14-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 18 11-02-08 23-02-08 18 11-02-08 23-02-08 18 11-02-08 23-02-08 18 11-02-08 29-02-08 18 01-03-08 19 11-02-08 29-02-08 18 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-	O O O O O O O O O O O O O O O O O O O	12-03-08 20-03-08 20-03-08 20-03-08 22-03-08 14-04-08 14-03-08 11-03-08 26-03-08 27-03-08 04-03-08 14-03-08	0 08-03-08 0 19-03-08 0 08-03-08 0 03-04-08 0 08-03-08 0 03-04-08 0 11-04-08 0 11-04-08	22-03-08 11-04-08 31-03-08 29-04-08 24-04-08	10 21		
Indept Description Control C	Pacified Notice T	Installation @Portion E	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	12-03-08 20-03-08 20-03-08 22-03-08 14-04-08 14-03-08 11-03-08 26-03-08 27-03-08 04-03-08 27-03-08 14-03-08	0 19-03-08 0 08-03-08 0 03-04-08 0 08-03-08 0 03-04-08 0 11-04-08 0 11-04-08	11-04-08 31-03-08 29-04-08 24-04-08	21	1 1 1	
20	22	23 27-02-08 20-03-08 23 27-02-08 20-03-08 25 27-02-08 20-03-08 48 27-02-08 14-04-08 17 27-02-08 14-03-08 14 27-02-08 11-03-08 29 27-02-08 26-03-08 Installation in Existing Roads @Portic 7 21-03-08 27-03-08 18 10-03-08 27-03-08 10 05-03-08 14-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 18 11-02-08 28-02-08 18 11-02-08 28-02-08 18 11-02-08 29-02-08 18 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 15-03-08 19 01-03-08 15-03-08 19 01-03-08 15-03-08 19 01-03-08 15-03-08 28-ting and Commissioning - Site Commissioning Tests (SCT) 139 10-04-07A 26-08-07 - SCT of SEC system @R8K & Port 12 09-08-07 - Site Commissioning Tests (SCT) 139 10-04-07A 26-08-07 - System Acceptance Tests (SAT) (9-08-07) - Operability Test (OPT) @R8K 30 22-10-07 20-11-07 - Operability Test (OPT) @R8K 30 22-10-07 20-11-07 - Operability Test (OPT) @R8K 14 29-10-07 15-11-07 - Training for R8 14 26-03-08 15-04-08 - Documentation for R8 Opening 252 25-07-07 01-04-08 - Training for R8 14 26-03-08 15-04-08 - Documentation for R8 Opening 252 25-07-07 01-04-08 - Training for R8 14 26-03-08 15-04-08 - Documentation for R8 Opening 252 25-07-07 01-04-08 - Training for R8 14 26-03-08 15-04-08 - Documentation for R8 Opening 252 25-07-07 01-04-08 - Training for R8 - Training for	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	20-03-08 20-03-08 22-03-08 14-04-08 14-03-08 11-03-08 26-03-08 27-03-08 04-03-08 27-03-08 14-03-08	0 19-03-08 0 08-03-08 0 03-04-08 0 08-03-08 0 03-04-08 0 11-04-08 0 11-04-08	11-04-08 31-03-08 29-04-08 24-04-08	21		
2	25 27 C C 16 C C C C 0 0 C C C C 23 P 28 25 25 25 25 25 25 25	23 27-02-08 20-03-08 25 27-02-08 22-03-08 48 27-02-08 14-04-08 17 27-02-08 14-03-08 14 27-02-08 11-03-08 29 27-02-08 26-03-08 Installation in Existing Roads @Portic 7 21-03-08 27-03-08 7 27-02-08 04-03-08 18 10-03-08 27-03-08 10 05-03-08 14-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 18 11-02-08 28-02-08 18 11-02-08 28-02-08 18 11-02-08 29-02-08 18 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 8 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 15-03-08 19 01-03-08 15-03-08 19 01-03-08 18-03-08 29 07-03-08 15-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 29 07-03-08 15-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 29 07-03-08 15-03-08 19 01-03-08 08-03-08 19 01-03-08 08-03-08 19 01-03-08 18-03-08 19 01-03-08 08-03-08 29 07-03-08 15-03-08 8 01-03-08 08-03-08 29 07-03-08 15-03-08 8 01-03-08 08-03-08 29 07-03-08 15-03-08 8 01-03-08 08-03-08 29 07-03-08 15-03-08 8 01-03-08 08-03-08 29 07-03-08 15-03-08 8 01-03-08 08-03-08 29 07-03-08 15-03-08 29 07-03-08 15-03-08 34 11-02-08 29-02-08 18 01-03-08 08-03-08 29 07-03-08 15-03-08 34 11-02-08 29-02-08 18 01-03-08 08-03-08 29 07-03-08 15-03-08 30 11-02-08 29-02-08 31 11-02-08 29-02-08 32 11-02-08 29-02-08 33 18-03-08 08-03-08 34 11-02-08 13-03-08 35 15-03-08 08-03-08 36 13-03-08 08-03-08 37 17-10-07 39 07-03-08 13-03-08 39 13-03-08 08-03-08 39 13-03-08	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	20-03-08 22-03-08 14-04-08 14-03-08 11-03-08 26-03-08 27-03-08 04-03-08 27-03-08 14-03-08	0 08-03-08 0 03-04-08 0 08-03-08 0 03-04-08 0 11-04-08 0 11-04-08	31-03-08 29-04-08 24-04-08			Install Cable Containment @Portion F
25	25 276-296 16-99 29 0	25 27-02-08 22-03-08 48 27-02-08 14-04-08 17 27-02-08 14-03-08 14 27-02-08 11-03-08 29 27-02-08 26-03-08 Installation in Existing Roads @Portion 7 21-03-08 27-03-08 7 27-02-08 04-03-08 18 10-03-08 27-03-08 10 05-03-08 14-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 Portion F - Stonecutters Bridge (SCB) Installaton @Portion F 13 11-02-08 23-02-08 18 11-02-08 28-02-08 6 01-03-08 10-03-08 10 01-03-08 10-03-08 110 01-03-08 10-03-08 111 01-03-08 18-03-08 111 01-03-08 18-03-08 111 01-03-08 18-03-08 111 01-03-08 18-03-08 111 01-03-08 18-03-08 111 01-03-08 19-03-08 111 01-03-08 15-03-08 111 01-03-08 15-03-08 111 01-03-08 15-03-08 111 01-03-08 18-03-08 111 01-03-08 111 01-03-08 111 01-03-08 111 01-03-08 111 01-03-08 111 01-03-08 111 01-03-08 111 01-0	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	22-03-08 14-04-08 14-03-08 11-03-08 26-03-08 26-03-08 27-03-08 04-03-08 27-03-08 14-03-08	0 03-04-08 0 08-03-08 0 03-04-08 0 11-04-08 0 11-04-08	29-04-08 24-04-08	10		■Electrical Installation @Portion E
44 70 0.06 1 6.0 6.0 1	43 27.5 ct 1.43.9.3 3.03.38 24.4 ct 4.5 5 1.5 5	48 27-02-08 14-04-08 17 27-02-08 14-03-08 14 27-02-08 11-03-08 29 27-02-08 26-03-08 Installation in Existing Roads @Portion 7 21-03-08 27-03-08 18 10-03-08 27-03-08 18 10-03-08 14-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 Portion F - Stonecutters Bridge (SCB) Installaton @Portion F 13 11-02-08 23-02-08 18 11-02-08 28-02-08 6 01-03-08 10-03-08 10 01-03-08 10-03-08 110 01-03-08 10-03-08 110 01-03-08 18-03-08 110 11-02-08 29-02-08 118 01-03-08 18-03-08 119 11-02-08 29-02-08 118 01-03-08 18-03-08 119 01-03-08 19-03-08 119 11-02-08 15-03-08 119 11-02-08 15-03-08 119 11-02-08 29-02-08 118 01-03-08 18-03-08 119 11-02-08 15-03-08 119 11-02-08 29-02-08 12 09-08-07 20-08-07 13 10-04-07A 26-08-07 14 09-08-07 20-08-07 15 SEC system @R8K & Portion Stone S	0 0 0 0 0 0 0 0 0 0 0 0 0	14-04-08 14-03-08 11-03-08 26-03-08 20-03-08 27-03-08 04-03-08 27-03-08 14-03-08	0 08-03-08 0 03-04-08 0 11-04-08 0 11-04-08	24-04-08			
17	17 270-28 4-00-28 0 16-400 5 16-400 5 44	17 27-02-08 14-03-08 14 27-02-08 11-03-08 29 27-02-08 26-03-08 17 21-03-08 27-03-08 7 21-03-08 27-03-08 18 10-03-08 27-03-08 10 05-03-08 14-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 18 11-02-08 23-02-08 18 11-02-08 28-02-08 6 01-03-08 10-03-08 10 01-03-08 10-03-08 10 01-03-08 18-03-08 11 01-03-08 18-03-08 12 01-03-08 18-03-08 13 11-02-08 29-02-08 14 01-03-08 18-03-08 15 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 29 07-03-08 15-03-08 29 07-03-08 15-03-08 20 07-03-08 15-03-08 20 07-03-08 15-03-08 20 07-03-08 15-03-08 20 07-03-08 15-03-08 20 07-03-08 15-03-08 20 07-03-08 15-03-08 20 07-03-08 15-03-08 20 07-03-08 13-03	0 0 0 0 0 0 0 0 0 0 0	14-03-08 11-03-08 26-03-08 27-03-08 04-03-08 27-03-08 14-03-08	0 03-04-08 0 11-04-08 0 11-04-08 0 12-04-08				
14 17 0 20 at 11 20 ft at 12 20 ft a	1	14 27-02-08 11-03-08 29 27-02-08 26-03-08 Installation in Existing Roads @Portion 7 21-03-08 27-03-08 7 27-02-08 04-03-08 18 10-03-08 14-03-08 14 15-03-08 14-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 18-03-08 4 15-03-08 18-03-08 18-03-08 18 11-02-08 23-02-08 18 11-02-08 23-02-08 18 11-02-08 23-02-08 18 11-02-08 29-02-08 18 01-03-08 19 11-02-08 29-02-08 18 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 19 01-03-08 18-03-08 18-03-08 1	0 0 0 0 0 0 0 0 0	11-03-08 26-03-08 Roads @Portion E 27-03-08 04-03-08 27-03-08 14-03-08	0 11-04-08 0 11-04-08 0 12-04-08	21-04-06			
22 27-239 28-230 0 13-240 15-240 44	Section Process Proc	29	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	26-03-08 Roads @Portion E 27-03-08 04-03-08 27-03-08 14-03-08	0 11-04-08	24-04-08			
Value Valu		Installation in Existing Roads @Portice 7	on E 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	Roads @Portion E 27-03-08 04-03-08 27-03-08 14-03-08	0 12-04-08				
7 27 20 20 20 20 20 20	7 27-12-00 27-20-06 0 17-20-06 29-20 18-percent 19-20-06 29-20 18-percent 19-20-06 19-	7 21-03-08 27-03-08 7 27-02-08 04-03-08 18 10-03-08 27-03-08 10 05-03-08 14-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 Portion F - Stonecutters Bridge (SCB) Installaton @Portion F 13 11-02-08 23-02-08 18 11-02-08 28-02-08 6 01-03-08 10-03-08 10 01-03-08 10-03-08 11 01-03-08 19-03-08 11 01-03-08 18-03-08 12 01-03-08 18-03-08 13 01-03-08 18-03-08 14 01-03-08 18-03-08 15 01-03-08 19-03-08 16 01-03-08 19-03-08 17 01-03-08 19-03-08 18 01-03-08 18-03-08 19 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 19 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18-03-08 18 01-03-08 18 01-03-08 18-03-08 18 01-03-08 18 01-03-08 18 01-03-08 18 01-03-08 18 01-03-08 18 01-03-08 18 01-03-08 18 01	0 0 0 0 0	27-03-08 04-03-08 27-03-08 14-03-08		10 00 00			
11	11 10 20 20 20 3 10 20 10 10 10 20 20 20	18 10-03-08 27-03-08 10 05-03-08 14-03-08 4 15-03-08 18-03-08 4 15-03-08 18-03-08 Portion F - Stonecutters Bridge (SCB) Installaton @Portion F 13 11-02-08 23-02-08 18 11-02-08 28-02-08 6 01-03-08 10-03-08 10 01-03-08 10-03-08 110 01-03-08 10-03-08 111 01-03-08 19-03-08 111 01-03-08 19-03-08 111 01-03-08 19-03-08 111 01-03-08 19-03-08 111 01-03-08 19-03-08 111 01-03-08 19-03-08 111 01-03-08 19-03-08 111 01-03-08 15-03-08 111 01-03-08 15-03-08 111 01-03-08 15-03-08 111 01-03-08 15-03-08 111 01-03-08 15-03-08 111 01-03-08 15-03-08 111 01-03-08 15-03-08 111 01-03-08 15-03-08 111 01-03-08 15-03-08 112 09-08-07 20-08-07 1139 10-04-07A 26-08-07 12 09-08-07 20-08-07 12 09-08-07 20-08-07 139 10-04-07A 26-08-07 14 09-08-07 23-10-07 15 System Acceptance Tests (SAT) (168 19-01-08 04-07-08 168 19-01-08 04-07-08 168 19-01-08 04-07-08 168 19-01-08 04-07-08 168 19-01-08 04-07-08 169 22-10-07 20-11-07 16 Operability Test (OPT) @R8K 16 19-01-08 21-07-08 17-10-07 189 18-05-06A 26-10-08 18-03-08 15-04-08 18-03-08 15-04-08 18-03-08 15-04-08 18-03-08 18-03-08 15-04-08 18-03-08	0 0 0 0	27-03-08 14-03-08		18-04-08	22		Electrical Installation @Portion E
Total Control 4 15 15 15 15 15 15 15	10	10	0 0	14-03-08	0 18-03-08				
4	4	## 15-03-08	0 0		0 31-03-08	18-04-08	21		■Install Traffic Control Field Devices @Portion E
A 15 0 Or 16 0 0 0 16 0 0 0 16 0 0 0 16 0 0 0 16 0 0 0 16 0 0 0 0 16 0 0 0 0 16 0 0 0 0 0 0 0 16 0 0 0 0 0 0 0 0 0 16 0 0 0 0 0 0 0 0 0 16 0 0 0 0 0 0 0 0 0 0 16 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	## 15 CO FACE 15	A	0	18-03-08					
Section Commissional Republic Section 1	Section Commissional Republic Section 1	National Color	0						
Installation Strategy Stra	Installation Strategy Stra	Installation			0 04-04-08	08-04-08	20		Install Vehicle Detector System @Portion E
13 1 11 12 02 0 20 20 0 0 25 02 0 0 0 0 0 0 0 0 14 1 1 1 1 1 1 1 1 1 1	13 11 12 28 28 28 28 28 3 29 29 30 29 29 29 29 29 29 29 2	13 11-02-08 23-02-08 18 11-02-08 28-02-08 6 01-03-08 06-03-08 10 01-03-08 10-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 8 01-03-08 19-03-08 19 01-03-08 19-03-08 19 01-03-08 19-03-08 19 11-02-08 29-02-08 18 01-03-08 19-03-08 19 01-03-08 19-03-08 19 01-03-08 19-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 9 07-03-08 15-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 09-08-07 20-08-07 SCT of SEC system @R8K & Port 12 09-08-07 Site Commissioning Tests @R8T 295 20-07-07 09-05-08 System Acceptance Tests @R8 (Name of the common of the		snage (SCB)					
11 11 12 20 20 20 20 20	18	18 11-02-08 28-02-08 6 01-03-08 06-03-08 10 01-03-08 10-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 8 01-03-08 19-03-08 19 01-03-08 19-03-08 19 01-03-08 19-03-08 19 11-02-08 15-03-08 19 11-02-08 15-03-08 19 11-02-08 15-03-08 19 01-03-08 18-03-08 19 07-03-08 15-03-08 19 07-03-08 15-03-08 19 07-03-08 15-03-08 19 07-03-08 15-03-08 19 07-03-08 15-03-08 19 07-03-08 15-03-08 19 07-03-08 18-03-08 19 07-03-08 18-03-08 19 07-03-08 15-03-08 19 07-03-08 18-03-08 19 07-03-08 18-03-08 19 07-03-08 15-03-08 19 07-03-08 18-03-08 19 07-03-08 18-03-08 19 07-03-08 18-03-08 19 07-03-08 18-03-08 15		23-02-08	0 25-02-08	08-03-08	14		Install Cable Containment @Portion F
Column C	0 10 30 8 0 30 8 0 7 40 8 10 40 40 10 46 30 10 10 10 10 10 10 10	6 01-03-08 06-03-08 10 01-03-08 10-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 8 01-03-08 19-03-08 19 01-03-08 19-03-08 19 01-03-08 19-03-08 19 11-02-08 15-03-08 19 11-02-08 15-03-08 19 11-02-08 15-03-08 19 01-03-08 18-03-08 19 07-03-08 18-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 8 01-03-08 04-07-08 9 27-07-07 23-10-07 9 System Acceptance Tests @R8 (with EOT) 44 08-06-08 21-07-08 9 07-03-08 9 27-07-07 01-04-08 9 17-10-07 9 Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 9 Operation and Maintenance Doct Documentation for R8 Opening 252 25-07-07 01-04-08 9 Training for R8 14 26-03-08 15-04-08 9 Operability Dates 0 20-11-07 0 09-08-08 9 Early Road Opening Areas (to be 42 20-07-07 30-08-07	L ~						
10 101-203 100-203 100-203 10 20-203 10-20-203 10	10 10.103-08	19 11-02-08 29-02-08 18 01-03-08 18-03-08 8 01-03-08 19-03-08 19 01-03-08 19-03-08 19 11-02-08 15-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 9 07-03-08 15-03-08 8 01-03-08 18-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 10-04-07A 26-08-07 SCT of SEC system @R8K & Port 12 09-08-07 20-08-07 Site Commissioning Tests (SCT) 139 10-04-07A 26-08-07 Site Commissioning Tests @R8T 295 20-07-07 09-05-08 System Acceptance Tests (SAT) (September 1996) System Acceptance Tests (SAT) (September 1996) 168 19-01-08 04-07-08 Operability Test (OPT) @R8K 30 22-10-07 20-11-07 SAT & OPT for SEC system @R8K 21-08-07 17-10-07 Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 Documentation for R8 Opening 252 25-07-07 01-04-08 Training for R8 14 29-10-07 15-11-07 Training for R8 14 29-10-07 15-11-07 Training for R8 14 26-03-08 15-04-08 Ompletion Dates 0 20-11-07 0 09-08-08 Early Road Opening Areas (to be 42 20-07-07 30-08-07	0						
10 10 10 10 10 10 10 10	10 10 10 10 10 10 10 10	18 01-03-08 18-03-08 8 01-03-08 08-03-08 19 01-03-08 19-03-08 19 11-02-08 15-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 9 07-03-08 15-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 12 09-08-07 20-08-07 9 09-05-08 9 27-07-07 09-05-08 9 27-07-07 23-10-07 9 System Acceptance Tests (SAT) (89 168 19-01-08 04-07-08 9 07-03-08 04-07-08 9 07-03-08 04-07-08 9 168 19-01-08 04-07-08 9 17-10-07 9 SAT & OPT for SEC system @R88 18 18-05-06 21-07-08 9 18-05-06 21-07-08 9 18-05-06 26-10-08	0	10-03-08	0 07-04-08	15-04-08	36		Install O&M Radio System @Portion F (Kiosk Z)
B 01-03-08 03-05-08 0 07-04-08 14 14 14 14 14 14 14 1	B	8 01-03-08 19-03-08 19 01-03-08 19-03-08 34 11-02-08 15-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 07-03-08 15-03-08 9 07-03-08 15-03-08 9 07-03-08 15-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 08-03-08 9 07-03-08 9 07-03-08 9 08-03-08 9 07-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-03-08 9 08-08 9 08-03-08							
19 01-02-08 19-02-08 0 01-02-08 0 0 02-09 0 03-09 07-04-08 14	19 01-00-98 190-00 0 05-90-00 0 190-90-00 0 290-90 14	19 01-03-08 19-03-08 34 11-02-08 15-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 9 10-04-07A 26-08-07 12 09-08-07 20-08-07 - Site Commissioning Tests (SCT) 139 10-04-07A 26-08-07 - Site Commissioning Tests (SAT) (SCT) 12 09-08-07 20-08-07 - Site Commissioning Tests (SAT) (SCT) - Site Commissioning Tests (SAT) (SCT) - Site Commissioning Tests (SAT) (SCT) - System Acceptance Tests (SAT) (SCT) - Operability Test (OPT) (SCT) - SAT & OPT for SEC system (SCT) - Operability Test (OPT) (SCT) - Operability Test (OPT) - Operability Test (SCT) - Operabilit							
34 11-02-08 15-02-08 0 0.50-08 0 0.50-08 0 13-03-08 0 13-03-08 0 13-03-08 0 13-03-08 0 13-03-08 0 13-03-08 0 13-03-08 0 13-04-08 36	1.102.08	34 11-02-08 15-03-08 19 11-02-08 29-02-08 18 01-03-08 18-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 esting and Commissioning Site Commissioning Tests (SCT) 139 10-04-07A 26-08-07 SCT of SEC system @R8K & Port 12 09-08-07 20-08-07 Site Commissioning Tests @R8T 295 20-07-07 09-05-08 System Acceptance Tests (SAT) (Section of the composition of the compo							
1 1 1 19 2 0	19 1 1-22 68 29 20 00 0 1 93 00 0 190 408 31 1 10 10 10 10 10 10 10 10 10 10 10 10	19 11-02-08 29-02-08 18 01-03-08 18-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 8 01-04-07A 26-08-07 139 10-04-07A 26-08-07 - SCT of SEC system @R8K & Port 12 09-08-07 20-08-07 20-08-07 - Site Commissioning Tests @R8T 295 20-07-07 09-05-08 - System Acceptance Tests (SAT) (89 27-07-07 23-10-07 - System Acceptance Tests @R8 (National Control of the system of							
18 01-03-08 18-03-08 0 0 02-04-08 19-04-08 32 19-04-09 35 19-04-09 15 07-05-09 15-03-09 0 15-03-09 0 03-04-08 11-04-08 33 19-04-09 15 07-05-09 0 03-04-08 11-04-08 33 19-04-09 15 07-05-09 19-04-09 15 07-05-09 19-04-09 1	10 10 30 18 30 30 0 12 04 08 12 04 08 32 0 12 04 08 36 12 04 08 36 12 04 08 36 12 04 08 36 12 04 08 36 12 04 08 36 12 04 08 36 12 04 08 36 12 04 08 36 12 04 08 36 12 04 08 08 04 04 04 04 04	18 01-03-08 18-03-08 9 07-03-08 15-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 8 01-03-08 08-03-08 9 siting and Commissioning 1 Site Commissioning Tests (SCT) 139 10-04-07A 26-08-07 12 09-08-07 20-08-07 12 09-08-07 20-08-07 12 09-08-07 20-08-07 139 27-07-07 09-05-08 14 29-07-07 23-10-07 15 System Acceptance Tests (SAT) (18 19-01-08 04-07-08 04-08 04-07-08 04-07-08 04-08 04-07-08 04-07-08 04-							
9 07-93-08	9 07-03-98 15-03-98 01 124-048 21-04-08 36 Install Visibility Sensor (@Protino F Install SCS System (Seque F 20 10-04-07A 12-06-07 10-04-07A	9 07-03-08 15-03-08 8 01-03-08 08-03-08 8 101-03-08 08-03-08 8 101-03-08 08-03-08 8 101-03-08 08-03-08 9 siting and Commissioning Tests (SCT) 139 10-04-07A 26-08-07 9 SCT of SEC system @R8K & Port 12 09-08-07 20-08-07 9 Site Commissioning Tests @R8T 295 20-07-07 09-05-08 9 27-07-07 23-10-07 9 System Acceptance Tests (SAT) (89 27-07-07 23-10-07 9 System Acceptance Tests @R8 (168 19-01-08 04-07-08 04-07-08 04-07-08 04-07-08 9 Operability Test (OPT) @R8K 30 22-10-07 20-11-07 9 SAT & OPT for SEC system @R8I 58 21-08-07 17-10-07 9 Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 09-08-08 04-07-08 09-08-08 04-07-08 09-08-08 09-08-08 09-08-08 09-08-08 09-08-08 09-08-07 00-							
Sisting and Commissioning Sisting Cardinal Sci	sting and Commissioning Tests (CCT) ⊕RBK 353 100-007A 75.0 60.7 7 7 10 04 07A 12 09 07 228 SCIT OF SEC system @RBK & Partion B 256 200-007 20-00.7 7 20-00.7 20 100-00.8 -90 SING Commissioning Tests (CCT) 70 20-00.8 -90 SING Commissioning Tests (CCT) 70 20-00.7 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 -90 -90 SING Commissioning Tests (CCT) 70 -90 SING Commissioning Tests (CCT) 70 -90 SING	## Site Commissioning Tests (SCT) 139	0						
Site Commissioning Tests (SCI) @RSK 120	Size Commissioning Tests (SCP) @RBK 1940-907 20-00-907 7 19-04-907 12-06-907 22-08 19-05-908 19	Site Commissioning Tests (SCT) 139	0	08-03-08	0 03-04-08	11-04-08	33		Install SEC System (Stage 1 & 2) @Portion F
199 19-04-07A 28-98-07 7 10-04-07A 12-08-07 -228	139 10-0-07A 20-86-07 7 10-6-07A 12-96-07 -228	139 10-04-07A 26-08-07 SCT of SEC system @R8K & Port 12 09-08-07 20-08-07 Site Commissioning Tests @R8T 295 20-07-07 09-05-08 System Acceptance Tests (SAT) (89 27-07-07 23-10-07) System Acceptance Tests @R8 (168 19-01-08 04-07-08) Operability Test (OPT) @R8K 30 22-10-07 20-11-07 SAT & OPT for SEC system @R8 (17-10-07) Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 Peration and Maintenance Documentation for R8K Opening 893 18-05-06A 26-10-08 Documentation for R8 Opening 252 25-07-07 01-04-08 Training for R8 14 29-10-07 15-11-07 Training for R8 15-04-08 Ompletion Dates 0 09-08-08 Early Road Opening Areas (to be 42 20-07-07 30-08-07		oning				111	
Section Sect	SCT of SEC system @RBK & Portion B 12	+ SCT of SEC system @R8K & Port 12	@R8K		BK .				
12 09-08-07 20-08-07 09-05-08 0 23-11-07 12-08-08 -43	12 09-08-07 20-08-07 01 13-08-07 10 10-08-08 -00	12				12-06-07	-228		
Size Commissioning Tests (@RBT Size Si	Size Commissioning Tests GRBT	+ Site Commissioning Tests @R8T 295 20-07-07 09-05-08 + System Acceptance Tests (SAT) (89 27-07-07 23-10-07 + System Acceptance Tests @R8 (168 19-01-08 04-07-08 + Operability Test (OPT) @R8K 30 22-10-07 20-11-07 + SAT & OPT for SEC system @R8I 58 21-08-07 17-10-07 + Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 peration and Maintenance Doct + Documentation for R8K Opening 893 18-05-06A 26-10-08 + Documentation for R8 Opening 252 25-07-07 01-04-08 + Training for R8K 14 29-10-07 15-11-07 + Training for R8 14 26-03-08 15-04-08 Ompletion Dates 0 20-11-07 0 09-08-08 + Early Road Opening Areas (to be 42 20-07-07 30-08-07				40.05.00			
295 20-07-07 09-05-08 0 23-11-07 12-06-08 43 System Acceptance Tests (SPI) ROBK 98 27-07-07 23-10-07 0 23-02-07 29-05-07 -161 System Acceptance Tests (SPI) Robbs	295 20-07-07 0.90-5-08 0 23-11-07 12.08-08 4-3 System Acceptance Tests (SAT) (SMI) (SMI) 89 27-07-07 23-10-07 0 23-02-07 29-05-07 -161 System Acceptance Tests (SAT) (Wilh EOT) System Acceptance Tests (SAT) (Wilh EOT) System Acceptance Tests (SAT) (Wilh EOT) Operability Test (OPT) (SRI) 30 22-10-70 0 14-05-07 20-00-08 -48 SAT & OPT for SEC system (SRIS Wilh EOT) 44 0.90-90 0 24-05-07 0 0 24-05-07 20-00-08 -89 Operability Test (SRIS Wilh EOT) 44 0.90-90 0 21-07-08 0 0 0-0-08 0 0-0-08 45 21-08-07 0 17-100 0 0 0-0-08 0 0-0-08 SS 21-08-07 0 10-09 0 0 0-0-08 0 0-0-08 SS 18-08-08 21-07-08 0 0 0-0-08 0 0-0-08 SS 18-08-08 21-08 0 0 0 0-0-08 SS 18-08-08 21-08 0 0 0 0-0-08 SS 18-08-08 0 0 0 0 0 0 0 Training for RIS 14 28-08-08 15-04-08 0 22-07-08 0 0 0 0 0 0 14 28-08-08 15-04-08 0 22-07-08 0 0 0 0 0 0 15 21-107 0 0 0 0 0 0 0 0 0	295 20-07-07 09-05-08 + System Acceptance Tests (SAT) (89 27-07-07 23-10-07 + System Acceptance Tests @R8 (\(\) 168 19-01-08 04-07-08 + Operability Test (OPT) @R8K 30 22-10-07 20-11-07 + SAT & OPT for SEC system @R8 58 21-08-07 17-10-07 + Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 **Peration and Maintenance Doct + Documentation for R8 Opening 893 18-05-06A 26-10-08 + Documentation for R8 Opening 252 25-07-07 01-04-08 + Training for R8K 14 29-10-07 15-11-07 + Training for R8 14 26-03-08 15-04-08 **Ompletion Dates 0 20-11-07 0 09-08-08 + Early Road Opening Areas (to be 42 20-07-07 30-08-07			0 13-05-07	10-05-08	-90		
System Acceptance Tests (SAT)	System Acceptance Tests (SAT) @RBK 89 27-07-07 23-10-07 0 23-02-07 29-05-07 1-61 System Acceptance Tests (RB (with EOT) 168 19-01-08 0 0 0 7-12-07 0 0 4-45 Operability Test (OPT) @RBK 58 21-08-07 17-10-07 0 24-05-07 20-09-08 -88 Operability Test (BBK) (with EOT) Decimentation for RBC Operability Test (BBK) (with EOT) Decimentation for RBC Operability Test (BBK) (with EOT) Bocumentation for RBC Operability (BBK) (With EOT) Bocumentation for RBC (BBK) (With EOT)	+ System Acceptance Tests (SAT) (89 27-07-07 23-10-07 + System Acceptance Tests @R8 (\(\) 168 19-01-08 04-07-08 + Operability Test (OPT) @R8K 30 22-10-07 20-11-07 + SAT & OPT for SEC system @R8F 58 21-08-07 17-10-07 + Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 peration and Maintenance Doct + Documentation for R8K Opening 893 18-05-06A 26-10-08 + Documentation for R8 Opening 252 25-07-07 01-04-08 + Training for R8K 14 29-10-07 15-11-07 + Training for R8 14 26-03-08 15-04-08 Ompletion Dates 0 20-11-07 0 09-08-08 + Early Road Opening Areas (to be 42 20-07-07 30-08-07			0 23-11-07	12-06-08	-43		
88	88	89 27-07-07 23-10-07 - System Acceptance Tests @R8 (v. 168 19-01-08 04-07-08 - Operability Test (OPT) @R8K 30 22-10-07 20-11-07 - SAT & OPT for SEC system @R8F 58 21-08-07 17-10-07 - Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 - Operability Test @R8 Opening 893 18-05-06A 26-10-08 - Documentation for R8 Opening 252 25-07-07 01-04-08 - Training for R8K 14 29-10-07 15-11-07 - Training for R8 14 26-03-08 15-04-08 - Ompletion Dates 0 20-11-07 0 09-08-08 - Early Road Opening Areas (to be 42 20-07-07 30-08-07				12 00 00	40		
168	168 19-01-08 04-07-08 0 07-12-07 07-08-08 4-43	168 19-01-08 04-07-08 1-0-07				29-05-07	-161		
Operability Test (OPT) ©RBK 30	Operability Test (OPT) @R8K 30 22-10-07 20-11-07 0 14-05-07 26-06-07 -161 SATA OPT for SEC system @R8K 58 21-08-07 17-10-07 0 24-05-07 20-09-08 -89 Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 0 08-06-08 20-09-08 0 Documentation for R8K Opening 883 18-05-06A 26-10-08 21 18-05-06A 22-02-10 -218 Documentation for R8K Opening 883 18-05-06A 26-10-08 21 18-05-06A 22-02-10 -218 Documentation for R8K Opening 152 252 25-07 01-04-08 9 30-09-07 23-06-08 67 Training for R8K 14 28-10-07 15-11-07 0 04-03-11 23-03-11 846 Training for R8 14 28-03-08 15-04-08 0 22-07-08 08-08-08 80 Minimal of R8K 09-08-08 0 01-07-09 32-06-08 80 O	Poperability Test (OPT) @R8K 30 22-10-07 20-11-07 SAT & OPT for SEC system @R8I 58 21-08-07 17-10-07 Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 Peration and Maintenance Doct Documentation for R8K Opening 893 18-05-06A 26-10-08 Documentation for R8 Opening 252 25-07-07 01-04-08 Training for R8K 14 29-10-07 15-11-07 Training for R8 14 26-03-08 15-04-08 Ompletion Dates 0 20-11-07 0 09-08-08 Early Road Opening Areas (to be 42 20-07-07 30-08-07	with EQ	ests @R8 (with	EOT)				
33 22-10-07 20-11-07 0 14-05-07 26-06-07 -161	30	30 22-10-07 20-11-07 SAT & OPT for SEC system @R8F 58 21-08-07 17-10-07 Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 Peration and Maintenance Documentation for R8K Opening 893 18-05-06A 26-10-08 Documentation for R8 Opening 252 25-07-07 01-04-08 Training for R8K 14 29-10-07 15-11-07 Training for R8 14 26-03-08 15-04-08 Ompletion Dates 0 20-11-07 0 09-08-08 Early Road Opening Areas (to be 42 20-07-07 30-08-07	0	04-07-08	0 07-12-07	07-08-08	-43		
S8 21-08-07 17-10-07 0 24-05-07 20-09-08 -89	SAT & OPT for SEC system @R8K 58	SAT & OPT for SEC system @R8I 58) @R8K					
58 21-08-07 17-10-07 0 24-05-07 20-09-08 8-89	Section Completion of RBK 21-08-07 0 24-05-07 20-09-08 8-99	58 21-08-07 17-10-07 Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 Peration and Maintenance Doct Documentation for R8K Opening 893 18-05-06A 26-10-08 Documentation for R8 Opening 252 25-07-07 01-04-08 Training for R8K 14 29-10-07 15-11-07 Training for R8 14 26-03-08 15-04-08 Ompletion Dates 0 20-11-07 0 09-08-08 Early Road Opening Areas (to be 42 20-07-07 30-08-07			0 14-05-07	26-06-07	-161		
Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 0 08-06-08 20-09-08 0 Documentation for R8K Opening 893 18-05-06A 28-10-08 21 18-05-06A 22-02-10 -218 Documentation for R8 Opening 893 18-05-06A 28-10-08 21 18-05-06A 22-02-10 -218 Documentation for R8 Opening 893 18-05-06A 28-10-08 21 18-05-06A 22-02-10 -218 Documentation for R8 Opening 893 18-05-06A 28-10-08 21 18-05-06A 22-02-10 -218 Documentation for R8 Opening 894 18-05-06A 28-10-08 21 18-05-06A 22-02-10 -218 Documentation for R8 Opening 895 18-05-06A 28-10-08 21-10-7 0 04-03-11 23-03-11 846 14 28-10-07 15-11-07 0 04-03-11 23-03-11 846 15 14 28-03-08 15-04-08 0 22-07-08 08-08-08 80 16 17 18-11-07 0 30-09-07 -51 17 18 18 18 18 18 19 19 18 18 19 19 19 18 18 10 19 19 18 18 10 19 19 18 18 11 19 19 18 18 12 19 19 18 18 13 19 19 19 18 14 19 19 18 18 15 19 19 18 16 12 19 19 18 17 18 19 19 19 18 19 19 19 18 18 19 19 19 18 18 19 19 19 18 18 19 19 19 18 19 19 19 18 19 19 19 18 19 19 19 18 19 19 19 18 19 19 19 18 19 19 19 18 19 19 19 18 19 19 19 19 19 18 19 10 19 19 18 10 19 19 10 19 19 18 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 19 10 19 19 1	Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 0 08-06-08 20-09-08 0 Descrition and Maintenance Documents & Training Documentation for R8K Opening 893 18-05-06A 26-10-08 21 18-05-06A 22-02-10 -218 Documentation for R8 Opening 252 25-07-07 01-04-08 9 30-09-07 23-06-08 67 Training for R8K 14 28-10-07 15-11-07 0 04-03-11 23-03-11 846 17 26-03-08 15-04-08 0 22-07-08 08-08-08 80 DIMIPICATION Areas (to be advised) 42 20-07-07 30-08-07 0 01-06-06 12-06-07 -161 Section Completion of R8K 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 Section Completion of R8R 23-03-07A 08-08-08 0 01-07-09 -163 DLP for R8K Work DLP for R8K Work 11-107 20-12-09 0 12-07-07 20-12-09 -163 DLP for R8K Work	Operability Test @R8 (with EOT) 44 08-06-08 21-07-08 peration and Maintenance Doct Documentation for R8K Opening 893 18-05-06A 26-10-08 Documentation for R8 Opening 252 25-07-07 01-04-08 Training for R8K 14 29-10-07 15-11-07 Training for R8 14 26-03-08 15-04-08 Documentation for R8 15 20-07-07 Documentation for R8 26-10-08 Documentation for R8 Documentation for R8 Documentation for R8 Documentation							
44 08-06-08 21-07-08 0 08-06-08 20-09-08 0 Decration and Maintenance Documents & Training B93 18-05-06A 26-10-08 21 18-05-06A 22-02-10 -218 Documentation for RB Opening 893 18-05-06A 26-10-08 21 18-05-06A 22-02-10 -218 Documentation for RB Opening 893 18-05-06A 26-10-08 9 30-09-07 23-06-08 67 Training for RBK 14 29-10-07 15-11-07 0 04-03-11 23-03-11 846 Training for RB 14 26-03-08 15-04-08 0 22-07-08 08-08-08 80 Dompletion Dates 0 20-11-07 0 30-09-07 -51 0 09-08-08 0 01-07-09 326 Early Road Opening Areas (to be advised) 42 20-07-07 30-08-07 0 01-06-08 12-06-07 -414 Section Completion of RBK 230 05-04-07A 20-11-07 0 0 05-04-07A 12-06-07 -161 Section Completion of RBRBT 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Defects Liability Period (DLP) for Works DLP for R8K Work	44 08-06-08 21-07-08 0 08-06-08 20-09-08 0 Decripation and Maintenance Documents & Training 893 18-05-06A 26-10-08 21 18-05-06A 22-02-10 -218 Documentation for 18K Opening 252 25-07-07 01-04-08 9 30-09-07 23-06-08 67 Training for RBK 14 29-10-07 15-11-07 0 04-03-11 23-03-11 846 Training for RBK 14 29-03-08 15-04-08 0 22-07-08 08-08-08 80 Description Dates 0 20-11-07 0 30-09-07 -51	44 08-06-08 21-07-08 peration and Maintenance Docu Documentation for R8K Opening 893 18-05-06A 26-10-08 Documentation for R8 Opening 252 25-07-07 01-04-08 Training for R8K 14 29-10-07 15-11-07 Training for R8 14 26-03-08 15-04-08 Documentation for R8 14 26-03-08 15-04-08 Documentation for R8 14 29-10-07 15-11-07 Documentation for R8 15-04-08 Documentation for R8 Documen	0		0 24-05-07	20-09-08	-89	iii	
Decementation for R8 Opening 25 25 07 07 01 04 08 08 08 08 08 08 08	Documentation for R8 Opening 250 25-07-07 01-04-08 9 30-09-07 23-06-08 80 20 10-07-09 15-11-07 0 04-03-11 23-03-11 846 10-08-08 10	Documentation for R8K Opening		- 1	0 00 00 00	00.00.00	0		
Bost	Documentation for R8K Opening Section Completion of R8K Section Completion of R8R	- Documentation for R8K Opening 893 18-05-06A 26-10-08 - Documentation for R8 Opening 252 25-07-07 01-04-08 - Training for R8K 14 29-10-07 15-11-07 - Training for R8 14 26-03-08 15-04-08 - Documentation for R8 - 14 26-03-08 15-04-08 - Documentation for R8 - 14 29-10-07 09-08-08 - Early Road Opening Areas (to be 42 20-07-07 30-08-07					U		
893	893	893 18-05-06A 26-10-08 Documentation for R8 Opening 252 25-07-07 01-04-08 Training for R8K 14 29-10-07 15-11-07 Training for R8 14 26-03-08 15-04-08 Description Dates 0 20-11-07 0 09-08-08 Early Road Opening Areas (to be 42 20-07-07 30-08-07			no a maining				
Documentation for R8 Opening 252 25-07-07 01-04-08 9 30-09-07 23-06-08 67 1-Training for R8K 14 29-10-07 15-11-07 0 04-03-11 23-03-11 846 1-Training for R8 14 26-03-08 15-04-08 0 22-07-08 08-08-08 80 15 20-07-07 20-11-07 0 30-09-07* -51 0 20-11-07 0 30-09-07* -51 0 09-08-08 0 01-07-09* 326 1-Early Road Opening Areas (to be advised) 42 20-07-07 30-08-07 0 01-06-06 12-06-07 -414 1-Section Completion of R8K 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 1-Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 1-Early Road Opening Areas (to be advised) 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 2-Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 3-Early Road Opening Areas (to be advised) 3-Early Road Opening Areas (to be advised) 4-Early Road Opening Areas (to	Documentation for R8 Opening 252 25-07-07 01-04-08 9 30-09-07 23-06-08 67	- Documentation for R8 Opening 252 25-07-07 01-04-08 - Training for R8K 14 29-10-07 15-11-07 - Training for R8 14 26-03-08 15-04-08 - Ompletion Dates 0 20-11-07 0 09-08-08 - Early Road Opening Areas (to be 42 20-07-07 30-08-07			21 18-05-064	22-02-10	-218		
252 25-07-07 01-04-08 9 30-09-07 23-06-08 67 Training for R8K 14 29-10-07 15-11-07 0 04-03-11 23-03-11 846 Training for R8 14 26-03-08 15-04-08 0 22-07-08 08-08-08 80 Training for B8 0 20-11-07 0 30-09-07* -51 0 09-08-08 0 01-07-09* 326 Early Road Opening Areas (to be advised) 42 20-07-07 30-08-07 0 01-06-06 12-06-07 -414 Section Completion of R8K 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Effects Liability Period (DLP) for Works DLP for R8K Work 751 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 DLP for R8T Work	252 25-07-07 01-04-08 9 30-09-07 23-06-08 67 Training for R8K 14 29-10-07 15-11-07 0 04-03-11 23-03-11 846 Training for R8 14 26-03-08 15-04-08 0 22-07-08 08-08-08 80 Impletion Dates 0 20-11-07 0 30-09-07 -51 0 09-08-08 0 01-07-09 326 Early Road Opening Areas (to be advised) 42 20-07-07 30-08-07 0 01-06-06 12-06-07 -414 Section Completion of R8K 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 offects Liability Period (DLP) for Works DLP for R8K Work DLP for R8K Work DLP for R8K Work	252 25-07-07 01-04-08 Training for R8K 14 29-10-07 15-11-07 Training for R8 14 26-03-08 15-04-08 Discription Dates 0 20-11-07 0 09-08-08 Early Road Opening Areas (to be 42 20-07-07 30-08-07	, -		7.0 00/1				
Training for R8K 14	Training for R8K 14	Training for R8K 14 29-10-07 15-11-07 Training for R8 14 26-03-08 15-04-08 Ompletion Dates 0 20-11-07 0 09-08-08 Early Road Opening Areas (to be 42 20-07-07 30-08-07			9 30-09-07	23-06-08	67		
14	14	14 29-10-07 15-11-07 Training for R8 14 26-03-08 15-04-08 Ompletion Dates 0 20-11-07 09-08-08 - Early Road Opening Areas (to be 42 42 20-07-07 30-08-07	9						
14 26-03-08 15-04-08 0 22-07-08 08-08-08 80 Ompletion Dates	14	14 26-03-08 15-04-08 ompletion Dates 0 20-11-07 0 09-08-08 - Early Road Opening Areas (to be 42 20-07-07 30-08-07	9	15-11-07	0 04-03-11	23-03-11	846		
Ompletion Dates 0	O	0 20-11-07 0 09-08-08 • Early Road Opening Areas (to be 42 20-07-07 30-08-07						1 11	
0	0	0 20-11-07 0 09-08-08 - Early Road Opening Areas (to be 42 20-07-07 30-08-07		15-04-08	0 22-07-08	08-08-08	80		
0	0	0 09-08-08 - Early Road Opening Areas (to be 42 20-07-07 30-08-07	0						
Early Road Opening Areas (to be advised) 42 20-07-07 30-08-07 0 01-06-06 12-06-07 -414 Section Completion of R8K 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 517 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 518 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 517 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 518 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 519 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 510 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 510 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 510 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 510 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 510 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T Sect	Early Road Opening Areas (to be advised) 42 20-07-07 30-08-07 0 01-06-06 12-06-07 -414 Section Completion of R8K 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 effects Liability Period (DLP) for Works DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 DLP for R8T Work	Early Road Opening Areas (to be 42 20-07-07 30-08-07	0					1111	
42 20-07-07 30-08-07 0 01-06-06 12-06-07 -414 - Section Completion of R8K 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 - Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 - Section Liability Period (DLP) for Works - DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 - DLP for R8T Work	42 20-07-07 30-08-07 0 01-06-06 12-06-07 -414 Section Completion of R8K 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 DLP for R8T Work	42 20-07-07 30-08-07	0	00.00.00		01-07-09*	326		▼Overall Completion of R8T&R8
- Section Completion of R8K 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 - Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 - Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 - DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 - DLP for R8T Work	Section Completion of R8K 230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 DLP for R8T Work		0			12.06.07	_/11/1		
230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161	230 05-04-07A 20-11-07 0 05-04-07A 12-06-07 -161 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 517 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 517 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 517 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 518 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 518 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 519 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 519 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 519 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 510 12-03-07A 08-08-08 0 12-03-07A 08-08-08 0 12-03-07A 08-08-08 08-08-08 08-08-08 08-08-08 08-08-08 08-08-08 08-08-08 08-08-08 08-08-08 08-08-08 08-		0 0 0 0	Areas (to be adv	0 01-00-00	14-00-0/	-414		
- Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 efects Liability Period (DLP) for Works - DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 - DLP for R8T Work	Section Completion of R8/R8T 516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 Section Completion of R8/R8T 516 12-03-07A 08-08-08 -51 Section Completion of R8/R8T DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 DLP for R8T Work	·	0 0 0 0	Areas (to be adv 30-08-07	0 05-04-074	12-06-07	-161		
516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 ◆	516 12-03-07A 08-08-08 0 12-03-07A 08-08-08 -51 ◆		0 0 0 0 2 advise	Areas (to be add 30-08-07 of R8K	2 30 07 07A	.= 00 07	.01		
Pricets Liability Period (DLP) for Works DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 DLP for R8T Work	#fects Liability Period (DLP) for Works DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 DLP for R8T Work		0 0 0 0 2 advise	Areas (to be add 30-08-07 of R8K 20-11-07	0 12-03-07A	08-08-08	-51		
- DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 -164 - DLP for R8T Work	DLP for R8K Work 761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 DLP for R8T Work		0 0 0 0 e advise	Areas (to be adv 30-08-07 of R8K 20-11-07 of R8/R8T		11 11 11	Ţ.		
761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 - DLP for R8T Work	761 21-11-07 20-12-09 0 12-07-07 20-12-09 -163 DLP for R8T Work		0 0 0 0 0 e advise	Areas (to be adv 30-08-07 of R8K 20-11-07 of R8/R8T 08-08-08	1/2				
- DLP for R8T Work	DLP for R8T Work		0 0 0 0 0 e advise	Areas (to be adv 30-08-07 of R8K 20-11-07 of R8/R8T 08-08-08	INS	20-12-09	-163		
			0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	Areas (to be adv 30-08-07 of R8K 20-11-07 of R8/R8T 08-08-08 d (DLP) for We					
			0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	Areas (to be adv 30-08-07 of R8K 20-11-07 of R8/R8T 08-08-08 d (DLP) for We		22-02-11	198	1 1 1	
		•	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	Areas (to be adv 30-08-07 of R8K 20-11-07 of R8/R8T 08-08-08 d (DLP) for We	0 12-07-07			•	
			0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	Areas (to be adv 30-08-07 of R8K 20-11-07 of R8/R8T 08-08-08 d (DLP) for We	0 12-07-07				

APPENDIX M COMPLAINT LOG

Appendix M - Complaint Log

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
40426	Butterfly Valley	26 April 2004	A public noise complaint was recently received by EPD. The complaint was related to the noise generated from the Route 8 – ENT site near Butterfly Valley at the night time on 21 April 2004. EPD subsequently referred the complaint to the Environmental Team (ET) Leader of the Project on 23 April 2004.	Noise at night time The information provided by the RSS indicated that no works were undertaken by the Contractor during the concerned period. The concerned noise might probably be due to a burglary case occurred at same night. Noise during day-time It is believed that the day-time noise complaint was due to the site formation works of the Project. Considering the powered mechanical equipment used at the Butterfly Valley and the echo effect of the valley, ET believe that the day-time construction noise from the site at Butterfly Valley might cause nuisance to the nearby resident to some extent, though there was no noise level exceedance at the Government Quarters during our routine monitoring in last three months. The Contractor agreed to implement mitigation measures, including good site practices, selecting quieter plant and working methods and reduction in numbers of noisy plant operating currently, in order to mitigate noise impacts at the NSRs.	Closed
40914	Garden Villa	13-Sep-04 (by EPD) 14-Sep-04 (by ET Leader)	Environmental Protection Department (EPD) received a public noise complaint on 13 September 2004 about construction noise generated from the Route 8 – Eagle's Nest Tunnel and Associated Works (R8-ENT) Project, nearby by Garden Villa at Tai Po Road, Sha Tin. EPD subsequently referred the complaint to the Environmental Team (ET) Leader of the Project on 14 September 2004. The complaint was about general construction noise generated from a construction site nearby Garden Villa at Tai Po Road, Sha Tin. As informed by EPD,	Environmental Permits A Construction Noise Permit (No. GW-RN0405-04) was obtained by the Contractor for the use of powered mechanical equipment (PME) in the concerned works area and use of TAR no.1 during restricted hours. Blasting Works According to the information provided by the Resident Site Staff (RSS), for carrying out blasting works, a blasting permit should be issued by the Mines Division of Civil Engineering and Development Department (CEDD), but not under the jurisdiction of EPD. The CNP issued by EPD only specified the use of PME but not the blasting works during restricted hours.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
			the complainant was particularly concerned of two issues: 1. The complainant was informed by the Contractor (Leighton – Kumagai Joint Venture) that blasting works would be conducted during restricted hours. He worried about the noise nuisance would be induced by the blasting works. 2. Noise nuisance from some site vehicles traveling on the Temporary Access Road (TAR no.1) near Garden Villa was noted by the complainant during restricted hours.	As advised by the RSS, the Contractor did intend to apply for a permit to the Mines Division of CEDD for blasting works during restricted hours. However, up to the time of preparation of this report, the Contractor still had not obtained the approval from the Mines Division and therefore, no blasting works were performed by the Contractor during restricted hours. Lise of TAR no.l According to Condition 3d of the above-mentioned CNP, there was restriction on the use of site vehicles traveling on TAR no.l. The usage of site vehicles on TAR no.l in a 2-week period before the date of complaint, i.e. 30th August to 12th September 2004 showed that the only vehicle type using TAR no.l for the concerned period was concrete truck and the number of vehicle pass was limited to 4 times per hour, which was in compliance with the above CNP's conditions. Regular noise monitoring was undertaken by ET at Garden Villa on 30th August and 6th September 2004 during restricted hours (1900 – 2300 hours). The monitoring results were 58.7 dB(A) and 58.6 dB(A), respectively, which were below the noise limit level of 60 dB(A). However, it should be noted that site vehicles were not used by the Contractor on TAR no.l during restricted hours on these two monitoring day. Based on the information obtained, the validity for the noise complaint in associated with night-time blasting works could not be concluded under ET's investigation, since no blasting works had been performed by the Contractor during restricted hours at the time of the report preparation. Also, it should be highlighted that for carrying out blasting works, permission should be obtained by Mines Division of CEDD, but not under the control of EPD. For the use of TAR no.l, the RSS's records showed that the number of vehicle pass in the period between 30th August and 12th September 2004 was complied with the CNP's conditions. It should be noted that only a maximum of 3 concrete trucks	

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
			Environmental Protection Department	passing the site entrance was recorded. Therefore, it was considered that the nuisance noted by the complainant was not due to the site vehicles adopted by the Contractor (LKJV). Nevertheless, the Contractor was reminded to ensure the compliance of the CNP conditions and adopt good site practice to minimize the construction noise.	
41021	Garden Villa	09-Oct-04 (by EPD) 21-Oct-04 (by ET Leader)	 (EPD) received a public noise complaint on 9 October 2004 about construction noise generated from the Route 8 – Eagle's Nest Tunnel and Associated Works (R8-ENT) Project, nearby by Garden Villa at Tai Po Road, Sha Tin. EPD subsequently referred the complaint to the Environmental Team (ET) Leader of the Project on 21 October 2004. The complaint was about nighttime construction noise generated from a construction site nearby Garden Villa at Tai Po Road, Sha Tin. As informed by EPD, the complainant was particularly concerned of two issues: Construction works undertaken by the Contractor (Leighton–Kumagai Joint Venture) were noted after 2300 hour. Some workers were noted leaving the site through Temporary Access Road (TAR) no.1 at around 2 am, causing nuisance to the residents in Garden Villa. 	According to the information provided by the RSS, no construction activity was undertaken in the nighttime period (2300 – 0700 hours) at the concerned site area. LKJV did admit that some vehicles had been operating at midnight for transporting LKJV's survey workers from the site. Inconsiderate behaviors were noted causing nuisance to Garden Villa residents: 1. Driving the vehicles too fast, which generated excessive engine noise; 2. Noise inside the vehicles (such as staff talking or radios) escaping through the open vehicle windows; and 3. Vehicle beeping horn to request the guards to open the gate. In order to rectify the situation, LKJV had notified the relevant staff with the receipt of the complaint and urged them to take appropriate measures when using TAR1 at night: 1. to drive slowly in order to reduce the engine noise, especially when approaching Garden Villa; 2. to roll up the vehicle windows to contain any noise from talking or radios; and 3. to prohibit beeping the vehicle horn for gate opening; instead, to park the car and approach the guard on foot.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
41023	Government Quarters (Butterfly Valley)	20-Oct-04 (by MHJV) 23-Oct-04 (by ET Leader)	A public complaint was received by the Engineer's Representative (ER) of Route 8 – Eagle's Nest Tunnel and Associated Works (R8-ENT) Project on 20 th October 2004. The complaint was raised by a resident of the Government Quarters at Caldecott Road, concerning dust generation as a result of the construction activities at Butterfly Valley. The ER subsequently referred the complaint to the Environmental Team (ET) Leader of the Project on 23 rd October 2004.	The complaint was considered valid based on: 1. ER's site observations; 2. ET's weekly site audit; and 3. 1-hr TSP exceedance record. Also, the sources of dust generation were identified as 1. 2 portions of the haul roads, one at Slope BV-S2 and one linking between South Portal Tunnel to Mui Kong Tsuen, were found to be dry. 2. Dust impact due to the haulage of excavated materials at the South Portal. Enhanced dust suppression measures had been implemented by the Contractor: • added rockfill to the haul road between South Portal Tunnel and the Gully fill area; • maintained watering to haul road at Slope BV-S2; • requested the fill material supplier to ensure the material was in a damp condition before leaving quarry; • provided for material not dampened at the Quarry to be directed to the wheel wash for water spray before entering the site; • when cleaning drill holes along slope BV-S4 to ensure adequate water was available for flushing to suppress dust emission; AND • provided damper stockpiles of cleared material at BV-S2 before loading. Based on ER's site observations, most of the above mitigation measures have been implementing by the Contractor. Also, an additional water browser was delivered to site on 29 th Oct 04. No significant fugitive dust emission has been found. During ET's site inspections on 27 th Oct and 3 rd Nov 2004, the situation was found improved. No deficiency relating to air quality impact was noted by ET during the two audit sessions. The results of air quality monitoring (1-hr and 24-hr TSP) in the period between 21 st Oct and 2 nd Nov 2004 were all found to be complied with the Action / Limit Levels.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
41124	Government Quarters (Butterfly Valley)	21-Nov-04 (by LKJV) 24-Nov-04 (by ET Leader)	A public complaint was received by the Contractor of Route 8 – Eagle's Nest Tunnel and Associated Works (R8-ENT) Project on 21 st November 2004 (Sunday). The complaint was concerned about excessive noise generation from construction machinery at Butterfly Valley on the same day. The Engineer's Representative (ER) subsequently referred the complaint to the Environmental Team (ET) Leader of the Project on 24 th November 2004.	According to the ER, the only construction activity at Butterfly Valley undertaken on 21 st Nov 04 was formation of access road near Slope BV-S2. The activity only involved operations of 1 no. of excavator and 1 no. of dump truck with grab, which complied with the condition stipulated in a valid CNP GW-RW0484-04, which was hold by the Contractor. Routine noise monitoring was conducted on 21 st and 28 th Nov 2004 at NM6. All the measured noise levels (48.5 to 56.4 dB(A)) were well below the noise limit level. In addition, the measurement results were within the baseline noise level. Therefore, the complaint was considered to be invalid. Nevertheless, the Contractor was reminded to ensure the compliance of the conditions stipulated in CNP. The Contractor was also recommended to adopt good site practice in order to minimize the construction noise.	Closed
41201	Government Quarters (Butterfly Valley)	01-Dec-04 (by MHJV & ET Leader)	A public complaint was received by the Engineer's Representative (ER) of Route 8 – Eagle's Nest Tunnel and Associated Works (R8-ENT) Project on 1 st December 2004. The complaint was raised by a resident of the Government Quarters at Caldecott Road, concerning dust generation at Butterfly Valley. The Environmental Team (ET) of the Project was informed with the complaint on the same day. The resident complained that a large portion of the excavated slopes was not properly covered, which caused dust nuisance to her.	The complaint was considered valid based on: 1. ER's site observations; 2. ET's weekly site audit Upon receipt of the complaint, a series dust control measures had been implemented by the Contractor, such as covering of the exposed slopes with appropriate sheeting, regular watering to the haul roads and excavated slope faces, etc. During the ET's weekly site audit on 08-Dec-04 together with the representative of HyD, IEC, ER and the Contractor, the above mitigation measures were observed. The idle slopes at BVS2 had been covered by tarpaulin sheeting and erosion mat. The left exposed slope surfaces at BVS2 were under excavation, thus being unable to be covered. According to the ER, the complainant has expressed his satisfaction to the site condition on 07-Dec-04, after the implementation of dust mitigation measures by the	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
				Contractor. However, owing to the prevailing of the dry season, the Contractor was reminded to ensure the dust control measures are effectively implemented.	
50125	Garden Villa (North Portal)	21-Jan-05 (by EPD) 25-Jan-05 (by ET Leader)	Environmental Protection Department (EPD) received a public noise complaint on 21 January 2005 about construction noise and dust generated from the Route 8 – Eagle's Nest Tunnel and Associated Works (R8-ENT) Project, nearby by Garden Villa at Tai Po Road, Sha Tin. EPD subsequently referred the complaint to the Environmental Team (ET) Leader of the Project on 25 January 2005. The complaint was about construction noise and dust generated from a construction site nearby Garden Villa at Tai Po Road, Sha Tin. The complainant was particularly concerned of two issues: 1. Noise from tunnel blasting work carrying out at around 7:30am and 10:00pm; and 2. Dump trucks without covering of canvas when leaving the construction site.	Noise from blasting For carrying out the blasting, the Contractor had obtained the permit from relevant authority. The ET's noise monitoring results did not show any exceedance for the measurement taken when blasting was in place. It should be highlighted that for carrying out blasting works, permission should be obtained by Mines Division of CEDD, but not under the control of EPD. In order to minimize the nuisance from the works, the Contractor was recommended: • To inform the residents around the area about the time of blasting in advance; and • To re-schedule the blasting time table, if possible, in order to avoid nuisance. Uncovered dump trucks In order to evaluate the situation, two inspections were carried out by the ET at Garden Villa on 27-Jan and 28-Jan-05 to identify the dump trucks leaving the site with uncovered load. On 27-Jan-05, 3 nos. of trucks, which were working for ENT Project, was noted by-passing Garden Villa without proper cover. Enhanced control (penalty system) was implemented by the Contractor after the inspection on 27-Jan. During the inspection on 28-Jan-05, 24 nos. of dump trucks for ENT Project were found leaving the site. No non-compliance was noted for the trucks working for ENT Project. LKJV was reminded to keep closely monitoring on the condition and the effectiveness of the proposed control measures.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
50308	Garden Villa (North Portal)	05-Mar-05 (by EPD) 08-Mar-05 (by ET Leader)	EPD received a public complaint on 5 March 2005 about construction noise and dust generated from the construction sites of Route 8 – Eagle's Nest Tunnel and Associated Works (R8-ENT) and Route 8 - Sha Tin Heights Tunnel and Approaches (R8-SHT), nearby by Garden Villa at Tai Po Road, Sha Tin. EPD subsequently referred the complaint to the Environmental Team (ET) Leader of the Project on 8 March 2005. The complaint was about construction noise and dust generated from the construction sites nearby Garden Villa at Tai Po Road, Sha Tin. The complainant was particularly concerned of the following issues: 1. Nighttime & Sunday construction noise 2. Noise from tunnel blasting at early morning and nighttime 3. Dust from construction activities	 Nighttime & Sunday construction noise no exceedance for noise monitoring restricted hour works were found complied with the CNPs records of vehicular trips on TAR1 did not show noncompliance of CNP conditions Noise from tunnel blasting at early morning and nighttime no exceedance for noise monitoring valid blasting permit had been obtained from CEDD blasting work is not under the jurisdiction of EPD Dust from construction activities dump trucks with uncovered / inadequately covered materials were observed leaving site no exceedance for TSP monitoring enhanced dust suppression measures had been implemented by the Contractor Conclusions The complaint against the dust issue (uncovered / inadequately covered dump trucks) was considered justifiable The Contractor was reminded to review the current checking system. Continuous spot checks would be performed by ET and RSS. 	Closed
50330	Garden Villa (TAR1)	30-Mar-05 (by EPD & ET Leader)	Environmental Protection Department (EPD) received a public complaint on 30 th March 2005 about construction noise from the sites of Route 8 – Eagle's Nest Tunnel and Associated Works (R8-ENT) near Garden Villa at Tai Po Road, Sha Tin. The complaint, which was lodged by a resident of Garden Villa on 29 th March 2005, was about the noise generated by heavy vehicles traveling in and out of the construction site near Garden Villa. According to the complaint, the noise was made from 7am onwards.	The site of concern was likely to be the Temporary Access Road no.1 (TAR1) connecting Tai Po Road and the construction sites of R8-ENT and Route 8 - Sha Tin Heights Tunnel and Approaches (R8-SHT). The time period of concern was within normal working hours (7am to 7pm) on a weekday not being holidays. According to the EM&A Manual, the criterion of construction noise in term of $L_{\rm eq}$ -30min within this period is 75 dB(A) for domestic premises. Since the commencement of the Project, no exceedance of daytime noise criterion of 75 dB(A) was recorded at Station AM3 (Garden Villa). During the 2-hour measurement period of the ad-hoc monitoring (0700-0900 hrs), all the measured noise levels ($L_{\rm eq}$ -30min) were below the daytime noise	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
				criterion of 75 dB(A). Based on the results of routine noise monitoring and the adhoc measurement on 1 st April 2005 at Garden Villa, no exceedance of daytime noise criterion of 75 dB(A) was recorded. The complaint lodged is therefore considered not justifiable. In order to minimize the nuisance generated by the vehicle use at Garden Villa, the Contractor has proposed to limit the frequency of trucks existing from TAR1 at a rate of one truck per minute during the time period of concern (7am to 8:30am).	
50415	Government Quarters	09-Apr-05 (by EPD) 15-Apr-05 (by ET Leader)	The complaint, which was lodged by a resident of 7/F, 38B, 8-10 Caldecott Road (Governmental Quarters) on 9 th April 2005, was about the noise generated by the construction works at the Butterfly Valley during daytime. The complainant mentioned that the instant noise level taken by himself was 78 to 82 dB(A). EPD subsequently referred the complaint to the Environmental Team (ET) Leader of the Project on 15 th April 2005. The time period of concern was within normal working hours (7am to 7pm) on a weekday not being public holidays. According to the EM&A Manual, the criterion of construction noise in term of L _{eq} -30min within this period is 75 dB(A) for domestic premises.	Governmental Quarters (Station NM6) is one of the designated noise monitoring stations in the EM&A programme. Routine monitoring is undertaken on a weekly basis in accordance with the EM&A Manual. Since the commencement of the Project, no exceedance of daytime noise criterion of 75 dB(A) was recorded at this station. Ad-hoc measurement was conducted at the complainant's premises on 22 Apr 05. The measured noise level was 69.0 dB(A), which was well below the daytime noise criterion of 75 dB(A). Based on the results of routine noise monitoring and the adhoc measurements conducted in the complainant premises, no exceedance of daytime noise criterion of 75 dB(A) was recorded. The complaint lodged is therefore considered not justifiable.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
50419	Government Quarters	15-Apr-05 (by EPD) 19-Apr-05 (by ET Leader)	The complaint was lodged by a resident of 8-10 Caldecott Road (Government Quarters) on 15 th April 2005 to EPD as well as the Chief Resident Engineer of the Project. EPD subsequently referred the complaint to the Environmental Team (ET) Leader of the Project on 19 th April 2005. The complainant mentioned that they had experienced quite a lot of noise emanating from the tunnel drilling area after 11pm over several nights and most particularly at the night of 14 th April 2005 and at 4am on 15 th April 2005.	The site of concern was likely to be the South Portal. For carrying out construction works at this area during restricted hours, two Construction Noise Permits (CNPs no. GW-RW0085-05 and GW-RW0086-06) were obtained by the Contractor in accordance with the requirements stipulated in Noise Control Ordinance. According to the information provided by the Resident Site Staff and the Contractor, the construction activities undertaken in the period between 11 th and 15 th April 2005 from 1900 to 0700 hours included drilling, breaking, trimming, set up of rock drill, installation of arch-rib and grouting. The powered mechanical equipment (PME) involved in the above works included backhoe, rock drill, loader, dumper, shot-crete machine, group pump, mobile platform and grout machine, which were covered by the CNPs. According to the routine monitoring results, for the time period between 2300-0700 hours, the measured noise levels exceeded the corresponding noise Limit Level of 50dB(A). However, the measured levels were found within the range of baseline level and below the average baseline level. Based on the routine noise monitoring results at Station NM6, the measured noise levels for the period between 2300-0700 hours were below the baseline noise level, which was comparable to the ambient level. According to the RSS's record, the PME items operated during the concerned period were found covered by the 2 CNPs hold by the Contractor. Based on the available information, there is not enough evidence to prove whether the complaint against nighttime construction noise generated in the concerned period (11 th to 15 th April 2005) is justifiable or not.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
50512	Yew Chung International School	12-May-05	On 11 May 05, a notice was sent to Yew Chung International School (YCIS) by the Contractor, providing their tentative blasting schedule on 12 May 05. It was shown that one of the blasting operations was scheduled at 09:30am, at when an examination was being held in YCIS. Upon receipt of the notice, a representative of YCIS lodged a complaint to the Contractor via the Project's hotline at 07:40 on 12 May 2005. The complainant expressed her objection to the blasting operation taken at 09:30am when the examination was taken place. The Contractor then agreed on one occasion only to delay the tunnel blast planned for 9:30am until 9:50am (i.e. 5 min after the examination). The complainant satisfied but did expect no future blasting during the examination period. According to the Engineer's Representative, the Contractor did not wish to make any commitment to ensure no blasting would be taken within the examination period.	A 1-day continuous noise measurement was conducted by the Environmental Team at Station NM1 on 26 May 05. According to the ER's record, two blasting operations were taken in the vicinity of YCIS on 26 May 05. One surface blast was taken at Butterfly Valley at 15:42 and one tunnel blasting was taken at South Portal at 16:56. The measurement results showed that the noise impact in term of Leq-5min and Leq-30min arising from the blasting operations was insignificant. No exceedance of construction noise criterion for examination period was recorded (Leq-30min < 65dB(A)). The complaint lodged was therefore considered not justifiable. However, in order to minimize the potential nuisance arising from the blasting noise and the siren sounds prior to blasting, the Contractor was recommended to consider scheduling the blasting operations beyond the examination periods.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
50610	Government Quarters	10-Jun-05	On 10 June 2005, the Resident Site Staff (Maunsell-Hyder Joint Venture) received a complaint from a resident of the Government Quarters at Caldecott Road. The complaint was concerned about the construction dust generation as a result of the construction activities of the Project at Butterfly Valley. The complainant had not specified which construction activities had contributed to the dust generation.	According to the RSS's preliminary investigation, it was considered that soil nailing at Slope BV-S2 was the dominant dust source and was likely to be the activity of concern. The dust suppression measures taken were found inadequate to control the dust dispersion from the works. Noticeable dust dispersion from the soil nailing work could be observed. **Corrective Actions** After the Contractor was notified by the RSS of the complaint, immediate action was taken by the Contractor on the same day (10 June 2005). The dust mitigation measures for the soil nailing were enhanced. An additional thicker cover was used. Also, continuous water spray was applied to suppress the dust emission. **Environmental Outcome** The RSS made a response to the complainant on 10 June 2005. The complainant was informed of the rectification actions taken by the Contractor. No further adverse comment was received from the complainant. **Conclusions** Based on the RSS's information, this complaint is considered to be valid and related to the construction activities of the Project. However, corrective action had been taken by the Contractor immediately and the situation was found improved.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
50712	A scattered house near South Portal and Tai Po Road Water Treatment Works Staff Quarters	12-Jul-05	On 12 July 2005, a resident, whose house is located near South Portal and Tai Po Road Water Treatment Works Staff Quarters, lodged a complaint to the Contractor via the Project's hotline at 11:40am. The complainant expressed his concern on the nuisance caused by the blasting works at early morning (before 07:00 hours) and late night (after 23:00 hours).	According to the information provided by the RSS, tunnel blasting works have been taken place in the concerned period in north bound tunnel from the Ventilation Adit towards the direction of the South Portal. Environmental Requirements In the EP, the EM&A Manual of the Project and the NCO, no requirement is specified for the control of blasting operation and the associated environmental impact, such as blasting noise. It should be highlighted that for carrying out blasting works, permission should be obtained by Mines Division of CEDD, but not under the jurisdiction of EPD. For carrying out the above-mentioned blasting operations, the Contractor has obtained a valid blasting permit from CEDD under the Dangerous Goods Ordinance (Cap. 295). Under this permit, the Contractor is allowed to carry out 24-hour blasting works within the designated area. Contractor's Actions Though the blasting noise is not under the control of any environmental related regulation and the Contractor is allowed to carry out 24-hour blasting, the Contractor would try to keep the blasts of concern undertaken between 07:00 to 23:00 hours. This arrangement could effectively reduce the potential nuisance to the residents within the more sensitive time period (23:00 to 07:00 on next day). Conclusions The subjected blasting operations were carried out by the Contractor under a valid blasting permit. The complaint lodged is therefore considered not justifiable.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
50809	Government Quarters (8-10 Caldecott Road)	09-Aug-05	On 9 August 2005, a resident of 8-10 Caldecott Road (Government Quarters) lodged a complaint to the Contractor via the Project's hotline at 14:30. The complainant expressed her concern on the nuisance caused by the blasting works undertaken at Butterfly Valley. Noise impact arising from the blasting works was one of the issues raised by the complainant.	An ad-hoc noise measurement was carried out on the roof of Government Quarters during a surface blast on 16 August 2005. According to the record of the RSS and the site observation, a surface blasting was undertaken at Butterfly Valley at around 15:38 on the monitoring day. The results show that the measured noise level in term of Leq-30min, i.e. 69.1 dB(A) during the surface blasting was well below the daytime construction noise criterion of 75 dB(A). Conclusion and Recommendation According to the results of ad-hoc noise measurement taken at Government Quarters on 16 August 2005, the measured noise levels (Leq-30min) did not exceed the noise criterion of 75 dB(A). In addition, the subjected blasting operations were carried out by the Contractor under a valid blasting permit. For the concern of noise impact, the complaint was considered not justifiable.	Closed
50830	Government Quarters (8-10 Caldecott Road)	30-Aug-05	The RSS received a public complaint from a resident of Government Quarters addressing two noise issues: 1. Noise nuisance caused by drilling works at Butterfly Valley; 2. Noise nuisance due to blasting 0045 hrs of 28 August 2005.	No exceedance was recorded for the routine noise monitoring at NM6 (Government Quarters). Ad-hoc noise measurement was conducted on 1 and 2 Sept 05. All measured noise levels complied with the noise criteria. Conclusion The complaint was considered not justifiable. However, the Contractor had taken proactive actions in order to minimize the nuisance of the residents, (1) to stop the rock breaking works at BVS2 and (2) to install temporary noise barriers for drilling works.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
50928	Government Quarters (8-10 Caldecott Road)	28-Sept-05	A resident of Government Quarters complaint about a blast undertaken at 0215hr on 28 Sept 05.	Environmental Monitoring After receiving the complaint, the ET carried out a continuous noise measurement at Station NM6 (Government Quarters) from 29 to 30 September 2005. All the measured noise levels in term of Leq-5min are close to the baseline noise level. The noise levels after correction of baseline levels were all below the noise criterion of 50 dB(A). Conclusion	Closed
				The subjected blasting operations were carried out by the Contractor under a valid blasting permit. In addition, no noise exceedance was recorded for the ad-hoc noise monitoring. The complaint lodged is therefore considered not justifiable.	
51025	Caldecott Hill (2 Caldecott Road)	25-Oct-05	A public complaint was received by the MWPMO of Highways Department on 25 October 2005. The complaint was subsequently refereed to the RSS and Environmental Team of Route 8 – Eagle's Nest Tunnel and Associated Works (R8-ENT) Project. The complaint was lodged by the management company of Caldecott Hill (No.2 Caldecott Road). It was about dust generation when construction vehicles, particularly dump trucks and concrete trucks, traveling along the Water Treatment Works (WTW) access road and its junction with Caldecott Road. According to the photos provided by the complainant, noticeable dust generation was observed during construction vehicles movement on the roads of concern.	Ad-hoc site inspections were carried out on 25 and 26 Oct 05. On 26 Oct 05, the WTW access road was observed dry. Deposition of dusty materials was noted. Significant dust generation was identified during vehicle movement. **Contractor's Actions** Mitigation actions were taken by the Contractor: 1. One labour was appointed to water spray the concerned road junction and clear up of dusty materials deposited on the WTW access road. 2. Regular watering on access road by hose pipe was performed to keep the road wet. 3. All vehicles would be wheel-washed and loads of dusty materials would be covered before leaving the site. **Conclusions** Based on the site observations, this complaint was considered to be valid and related to the Project works. However, enhanced dust mitigation measures were taken by the Contractor and the situation was found improved.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
51031	Po Leung Kuk Choi Kai Yau School	31-Oct-05	The resident site staff (MHJV) of R8-ENT received a complaint from the Principal of PLKCKY School. She commented that the blasting noise (nighttime and daytime) at Butterfly Valley became louder than before.	An ad-hoc noise measurement was taken by ET on 5 Nov 05 to evaluate the noise impact due to daytime surface blasting at the BV. The measurement results revealed that there has been no exceedance of noise level criteria. The complaint was therefore considered not justifiable.	Closed
51101	Butterfly Valley (Government Quarters)	1-Nov-05	 On 1 Nov 05, the Resident Site Staff received a complaint from a resident of the Government Quarters. On 2 Nov 05, a complaint of similar natures and same location was received by the Environmental Protection Department. The complainant was concerned about the following environmental issues: 1. Noise nuisance due to tunnel blasting works undertaken at midnights and in early mornings (3am to 5am); 2. Noise nuisance due to operation of a generator after 11pm; 3. Construction dust and daytime noise due to processing and stockpiling of crushed rocks at Butterfly Valley; 4. Noise nuisance due to works outside tunnel in the early morning of 2 Nov 05. 	Item 1: Noise nuisance due to tunnel blasting For carrying out the above-mentioned blasting operations, the Contractor has obtained a valid blasting permit from CEDD. Under this permit, the Contractor is allowed to carry out 24- hour blasting works. As advised by the Contractor, all the blasting operations had been completed by 12 Nov 05. Item 2: Noise due to operation of a generator after 11pm According to the Construction Noise Permit issued by EPD, one generator was allowed to be operated after 11pm at South Portal area outside the tunnel. In view of the provision of acoustic enclosure and the separation distance from the generator to Government Quarters (around 300m), the noise impact arising from this generator onto the residents of the Quarters was believed to be insignificant. During the ET's investigation on 11 Nov 05, no engine-like noise generated from the construction site could be identified. Item 3: Dust and noise due to handling of crushed rocks No noise exceedance was recorded. During the weekly site inspections, deficiencies regarding inadequate dust mitigation measures for the crushed rock processing and stockpiling were occasionally observed. Dry / uncovered stockpiles and dust emissions from crushed rocks handling were sometimes noted. Item 4: Noise from works out of tunnel in morning of 2 Nov 05 According to the RSS's site records, there has been no activity outside the tunnel in the early morning of 2 November 2005. Work was undertaken deep inside the tunnel during the concerned period. The mentioned noise nuisance might not be related to R8-ENT Project. An ad-hoc noise measurement was carried out by ET from 8 to 10 November 2005 in order to evaluate the noise at Quarter's residents and no exceedance was recorded.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
				Conclusion Based on the information obtained, environmental monitoring results and site observations, this complaint was considered not justifiable, except for the concern of dust nuisance due to crushed rock processing.	
51205	Caldecott Road junction	5-Dec-05	The complaint was lodged by the management company of Villa Carlton. The complainant mentioned that several complaints from the occupants of Villa Carlton were received, against the dust emission when they drove to Kowloon via the Caldecott Road Junction. She also considered that the amount of water spraying by the Contractor was insufficient to suppress dust emission at Caldecott Road Junction.	A similar complaint (Log no. 51025) was received on 25 Oct 05 from Caldecott Hill. Significant dust emission was noted when construction vehicles traveling along the WTW access road and its junction with Caldecott Road. With implementation of enhanced dust mitigation measures, the situation was found improved and satisfactory. Site Observations Since Nov 05, in order to observe the Contractor's actions taken for the above-mentioned complaint, the area of interest was included during the weekly environmental audit. No deficiency had been noted at this area during the audit. After receiving this new complaint (Log no.51205), several ad-hoc site inspections were carried out on 6, 8 and 14 Dec 05. In addition, the RSS of the Project had carried out daily checking of the condition of the Caldecott Road Junction. Sufficient dust mitigation measures had been implemented by the Contractor. The condition was found satisfactory. Therefore, this complaint was considered not justifiable. However, it is noted that the Contractor had stepped up dust mitigation measures to further improve the condition at Caldecott Road junction.	Closed

Log Ref.	Location of Concern	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
60204	Garden Villa	4-Jan-06 (by ETL)	A public complaint was received by the Environmental Protection Department on 3 January 2006. The complaint was subsequently referred to the Environmental Team of Route 8 – Eagle's Nest Tunnel and Associated Works (R8-ENT) Project on 4 January 2006. According to EPD's information, the complaint was lodged by a complainant, who walked along Tai Po Road on 1-2 January 2006. The following information was given by EPD for our investigation: • Time of concern: 1-2 January 2006 (Daytime) • Suspected site area of concern: ENT's Toll Plaza and Administration Building. • Dust and noise nuisance was noted by the complainant when he passed Garden Villa. • Noise from wood saw and crane or alike was noted.	According to the Contractor's information, construction activities were carried out on 1 and 2 Jan 06, including: • Erection and dismantling of formwork • Fixing water pipe All the equipment operated by the Contractor on 1-2 Jan 06 complied with the permissible equipment stated in the CNP. On 1 Jan 06, noise monitoring was carried out. All the results complied with the noise criterion. B. Construction Dust Impact Erection and dismantling of formwork and fixing water pipe were considered not dust emissive in nature. For stockpiles of materials in Toll Plaza area, dust mitigation measures had been implementing by the Contractor. The condition in term of dust control was found satisfactory during the audit sessions on 4 and 11 Jan 06. Since December 2005, all TSP monitoring results complied with the Action / Limit Level. Conclusion Based on the information given, site observations and environmental monitoring results, this complaint was considered not justifiable. Nevertheless, the Contractor was reminded to adopt good site practice to minimize the environmental impacts at the nearby sensitive receivers	Closed
