

CONTRACT NO: KL/2009/01

SITE FORMATION FOR KAI TAK CRUISE TERMINAL DEVELOPMENT

QUARTERLY ENVIRONMENTAL MONITORING & AUDIT REPORT

- DECEMBER 2011 TO FEBRUARY 2012 -

CLIENT:

Penta-Ocean Construction Co., Ltd.

Unit 601, K. Wah Centre, 191 Java Road, North Point, Hong Kong

PREPARED BY:

Lam Environmental Services Limited

11/F Centre Point 181-185 Gloucester Road, Wanchai, H.K.

Telephone: (852) 2882-3939 Facsimile: (852) 2882-3331 E-mail: <u>info@lamenviro.com</u> Website: <u>http://www.lamenviro.com</u>

CERTIFIED BY:

Raymond Dai Environmental Team Leader

DATE:

27 March 2012



FAX MESSAGE

Priority	🗆 normal / 🗆 urgent		
То	Lam Environmental Services Limited	Ref. No.	MCLF3048
Country		Email	raymonddai@lamenviro.com
Attn.	Mr. Raymond Dai	Date	27 March 2012
From	Joseph Poon	No. of Pages	1 (Incl. this page)
C.c. To	Mr. Barry Wong (Scott Wilson Limited)	Email	barry.wong@scottwilson.com.hk
	Mr. K. Y. Shin (Civil Engineering and Development Department)	Email	kyshin@cedd.gov.hk
	Mr. Stephen Cheng (Scott Wilson Limited)	Email	stephen.cheng@scottwilson.com.hk
	Mr. Andrew Tam (Scott Wilson Limited)	Email	andrew.tam@scottwilson.com.hk
	Mr. Perry Yam (Penta-Ocean Construction Company Limited)	Email	perry.yam@pentaocean.com.hk
Subject	Agreement No. CE 19/2009 (EP) Dredging Works for Proposed Cruise Terminal a Quarterly Environmental Monitoring & Audit Re February 2012	at Kai Ta	ak —

We refer to the revised Quarterly EM&A Report for December 2011 to February 2012 that we received through email on 27 March 2012 and are pleased to confirm we have no further comment on the report.

Should you require further information, please feel free to contact us.

Best regards,

Joseph Poon Independent Environmental Checker

JP/CY/by

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us immediately.

(If you do not receive all pages, please fax response or phone +852-24508238.)



TABLE OF CONTENTS

EXE	CUTIV	E SUMMARY	III
1.	INTRO	DDUCTION	1
	1.1 1.2	Scope of the Report Structure of the Report	
2.	PROJ	ECT BACKGROUND	2
	2.1 2.2 2.3 2.4	Background Scope of the Project and Site Description Project Organization Principal Work and Activities	2 2
3.	MONI	TORING REQUIREMENTS	4
	3.1. 3.2.	Noise Monitoring Water Quality Monitoring	
4.	MONI	TORING RESULTS	6
	4.1. 4.2. 4.3.	Water Monitoring Results Water Quality Surveillance System Dredging and Disposal	6
5. NOI		PLIANCE AUDIT, REVIEW OF THE REASONS FOR AND THE IMPLICATIONS OF PLIANCE	9
	5.1. 5.2. 5.3. 5.4. 5.5. 5.6.	Noise Monitoring Water Quality Monitoring Water Quality against the Tidal Movement along Victoria Harbour Natural Variation Comparison Site Audit Summary of action taken in the event of and follow-up on non-compliance	9 9 10 12
6.		PLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION	
7.	CONC	CLUSION	14



LIST OF TABLES

- Table I
 Principle Work Activities in the Reporting Quarter
- Table 2.2
 Contact Details of Key Personnel
- Table 2.4
 Principle Work Activities during the Reporting Quarter
- Table 3.1Noise Monitoring Stations
- Table 3.2
 Marine Water Quality Stations for Water Quality Monitoring
- Table 3.3 Water Quality Monitoring Frequency and Parameters
- Table 4.1.1 Summary of Exceedances Recorded in the Reporting Quarter
- Table 4.2.1 Compliance with EP Conditions in the Reporting Quarter
- Table 4.2.2
 Waste Quantities Related To Dredging Works
- Table 5.4
 Upper Bound of Natural Variation Levels at Water Monitoring Stations
- Table 6.1
 Environmental Complaints Log
- Table 6.2Cumulative Statistics on Complaints
- Table 6.3
 Cumulative Statistics on Successful Prosecutions

LIST OF FIGURES

<u>Figure 2.1</u>	General Layout
Figure 2.2	Project Organization Chart
Figure 3.1	Layout of Environmental Monitoring Stations
Figure 4.1	Layout of Monitoring Stations for Water Quality Surveillance System

LIST OF APPENDICES

- Appendix 2.1 Implementation Schedule of Environmental Mitigation Measures
- Appendix 3.1 Action and Limit Levels
- Appendix 4.1 Graphical Presentation of Water Quality Monitoring Results
- Appendix 4.2 Graphical Presentation of Water Quality Surveillance System
- Appendix 5.1 Event and Action Plan
- <u>Appendix 5.2</u> Graphic Presentation of SS Results against to Tidal Movement along Victoria Harbour
- <u>Appendix 5.3</u> Graphic Presentation of Water Quality Result with respect to Local Variation
- Appendix 7.1 Construction Programme



EXECUTIVE SUMMARY

i. This is the seventh Quarterly Environmental Monitoring and Audit (EM&A) Report – December 2011 to February 2012 for the Site Formation for Kai Tak Cruise Terminal Development under Contract No. KL/2009/01. Dredging of marine sediment has been commenced since 28 June 2010 while removal and reconstruction of existing seawall has been commenced since 22 November 2010. This report presents the environmental monitoring findings and information recorded during the period from December 2011 to February 2012.

Construction Activities in the Reported Period

ii. During the reporting period, the principle work activities are summarized as below:

Table I Principle Work Activities in the Reporting Quarter

	December 2011		January 2012		February 2012
•	Dredging of marine sediment;	•	Dredging of marine sediment;	•	Dredging of Marine Sediment;
•	Removal of Existing Seawall;	•	Removal of Existing Seawall;	•	Removal of Existing Seawall;
•	Fabrication and installation of silt curtain for seawall removal;	•	Fabrication and installation of silt curtain for seawall removal;	•	Fabrication and installation of silt curtain for seawall removal;
•	Maintenance of Silt Curtain and Silt Screens;	•	Maintenance of Silt Curtain and Silt Screens;	•	Maintenance of Silt Curtain and Silt Screens;
•	Sorting of inert C&D material from existing seawall;	•	Sorting of inert C&D material from existing seawall;	•	Sorting of inert C&D material from existing seawall;
•	Disposal of surplus fill material off-site; and	•	Disposal of surplus fill material off-site; and	•	Disposal of surplus fill material off-site; and
•	Reconstruction of New Seawall	•	Reconstruction of New Seawall	•	Reconstruction of New Seawall

Noise Monitoring

iii. Due to the non-existence of planned NSRs during the reporting quarter, no noise monitoring was required to be conducted at the planned noise monitoring locations NM1 and NM2.

Water Quality Monitoring

- iv. Water quality monitoring was conducted at 6 designated monitoring stations namely WSD9, WSD10, WSD15, WSD17, WSD19 and WSD21. SS exceedance was found on the 20 February 2012 at WSD15 during flood tide. Investigation found that the exceedance was not related to the Project works.
- v. Supplementary to Baseline Water Quality Monitoring Report Review of Action and Limit Levels (Revision 1.2) was submitted to EPD on 13 October 2011. With respect to the EPD's no comment on the new Action and Limit Levels for water monitoring on 19 October 2011, the new set Action and Limit Levels for turbidity and SS was started to use from 19 October 2011.

Water Quality against the Tidal Movement along Victoria Harbour



vi. In the recorded upstream exceedance in reporting quarter, no apparent rising SS level in ownstream across the Victoria Harbour after passing the project location. It concluded that no water quality impact was arising from the Project works.

Natural Variation Comparison

vii. Based on the determination of upper bound of the natural variation levels from the Supplementary to Baseline Water Quality Monitoring Report, all SS results in reporting month were well within the upper bound of natural variation levels. For the SS exceedance recorded at WSD15 on 20 February 2012, it was upstream of the project site area and no apparent rising SS level downstream across the Victoria Harbour after passing the project location. It definitely concluded that the exceedance was not related to the Project works.

Water Quality Surveillance System

- viii. With reference to the upper bound of natural variation levels and water quality surveillance conducting in reporting period, it shows no fluctuation over the upper bound and hence this further supports such exceedance is not caused by dredging activities.
- ix. Since the investigations found that the exceedance recorded in the reporting quarter was not related to the Project, it was concluded that all necessary steps under Event and Action Plan had been taken. The details of Event and Action Plans and Notification of Exceedance summarizing the finding of investigation, possible causes can be referred to the Monthly EM&A Reports.

Waste Management

- x. In this reporting quarter, there was marine sediment (Type 1 Open Sea Disposal) disposed to South Cheung Chau Spoil Disposal Area denoted "KTCT-1" and "KTCT -2". The dredging and disposal of the sediment (Type 1 – Open Sea Disposal (Dedicate Sites) and Type 2 – Confined Marine Disposal) to East Sha Chau Contaminated Mud Disposal Site – Pit IVc was completed in June 2011.
- xi. There were 2,800m³ inert surplus fill materials and 45m³ non-inert C&D material related to dredging works were disposed off site in this reporting quarter.

Complaints, Notifications of Summons and Successful Prosecutions

xii. No complaint, notification of prosecutions or summons was received in the reporting quarter.



1. INTRODUCTION

1.1 Scope of the Report

- 1.1.1. Lam Environmental Services Limited (LES) has been appointed to work as the Environmental Team (ET) for dredging works to implement the Environmental Monitoring and Audit (EM&A) programme for the Site Formation for Kai Tak Cruise Terminal Development under Contract No. KL/2009/01. Dredging of marine sediment and removal and reconstruction of existing seawall were commenced on 28 June and 22 November 2010 respectively.
- 1.1.2. This report presents the environmental monitoring and auditing work carried out in accordance to the Section 10.7 under Environmental Monitoring and Audit (EM&A) Manual.
- 1.1.3. This report documents the finding of EM&A works during the quarter from December 2011 to February 2012.

1.2 Structure of the Report

- Section 1 *Introduction* details the scope and structure of the report.
- Section 2 *Project Background* summarizes background and scope of the Project, site description, project organization and contact details of key personnel during the reporting period.
- Section 3 *Monitoring Requirements* summarizes all monitoring parameters, monitoring locations, monitoring frequency, duration and action plan.
- Section 4 *Monitoring Results* summarizes the monitoring results obtained in the reporting period.
- Section 5 Compliance Audit, Review of the Reasons for and the Implication of Non-compliance summarizes the auditing of monitoring results, all exceedances environmental parameters, review the reasons for and the implication of non-compliance.
- Section 6 *Complaints, Notification of summons and Prosecution* summarizes the cumulative statistics on complaints, notification of summons and prosecution

Section 7 Conclusion



2. PROJECT BACKGROUND

2.1 Background

- 2.1.1. The former Kai Tak Airport located in the south-eastern part of Kowloon Peninsula was the international airport of Hong Kong. The Kai Tak Airport had come into operations since 1920s. The operation of the Kai Tak Airport was ceased and replaced by the new airport at Chek Lap Kok in July 1998. After closure, the disused airport site has been occupied by various temporary uses, including a golf driving range on the runway area.
- 2.1.2. In 2002, the Chief Executive in Council approved the Kai Tak Outline Zoning Plans (No. S/K19/3 and S/K21/3) to provide the statutory framework to proceed with the South East Kowloon Development at the former Kai Tak Airport. However, following the judgment of the Court of Final Appeal in January 2004 regarding the Harbour reclamation, the originally proposed development which involves reclamation has to be reviewed. The Kai Tak Planning Review (KTPR) has resulted with a Preliminary Outline Development Plan (PODP) for Kai Tak in October 2006. Subsequently, the Administration announced in October 2006 a plan to implement a cruise terminal at Kai Tak, as part of the development.
- 2.1.3. Development of the cruise terminal at Kai Tak would require dredging at the existing seawall at the southern tip of the former Kai Tak Airport runway for construction of a quay deck structure for two berths, and dredging the seabed fronting the new quay to provide necessary manoeuvring basin. The general layout of the proposed cruise terminal construction is shown in *Figure 2.1*.
- 2.1.4. The current Project involves a dredging operation exceeding 500,000m³ for construction and operation of the proposed cruise terminal at Kai Tak and is therefore classified as a Designated Project under Item C.12, Part I, Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO). An Environmental Impact Assessment (EIA) Study for the Project has been undertaken in accordance with the EIA Study Brief (No. ESB-159/2006) and the Technical Memorandum on Environmental Impact Assessment Process (EIAO-TM).

2.2 Scope of the Project and Site Description

- 2.2.1. The scope of the Project comprises:
 - Dredging of marine sediment of about 700,000m³ from the existing seabed (Stage 1 dredging) in the Harbour area off the southern tip of the former Kai Tak Airport runway to provide the necessary water depth within the manoeuvring area for cruise vessels; and
 - Removal of existing seawall of about 322,300m³ by dredging at the southern tip of the former Kai Tak Airport runway for cruise berth construction.

2.3 Project Organization

2.3.1. Kowloon Development Office of Civil Engineering and Development Department is the overall project controller. For the construction phase of the Project, Project Engineer, Contractor,



Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.

2.3.2. The proposed project organization and lines of communication with respect to environmental protection works are shown in <u>Figure 2.2</u>. Key personnel and contact particulars are summarized in *Table 2.2*:

Party	Role	Name	Post	Contact No.	Contact Fax
Civil Engineering and Development Department (Kowloon Development Office)	Project Proponent	Ir. KY Shin	Senior Engineer	2301 1461	2301 1277
URS /	Engineer's	Mr. Stephen Cheng	Chief Resident	2148 7638	2148 7277
Scott Wilson Limited	Representative		Engineer		
Penta-Ocean Construction	Contractor	Mr. H. Taguchi	Project Manager	2148 7238	2148 7138
Company Limited		Mr. Warren Tse	Site Agent		
		Mr. Perry Yam	Environmental Officer		
Fugro (HK) Limited	Independent Environmental Checker (IEC)	Mr. Joseph Poon	Independent Environmental Checker (IEC)	2450 8238	2450 6138
Lam Environmental Services Limited	Environmental Team Leader	Mr. Raymond Dai	Environmental Team Leader (ETL)	2882 3939	2882 3331

 Table 2.2
 Contact Details of Key Personnel

2.4 Principal Work and Activities

2.4.1. During this reporting quarter, the principal work activities are summarized in **Table2.4**.

 Table 2.4
 Principle Work Activities during the Reporting Quarter

	December 2011		January 2012		February 2012
•	Dredging of marine sediment;	•	Dredging of marine sediment;	•	Dredging of Marine Sediment;
•	Removal of Existing Seawall;	•	Removal of Existing Seawall;	•	Removal of Existing Seawall;
•	Fabrication and installation of silt curtain for seawall removal;	•	Fabrication and installation of silt curtain for seawall removal;	•	Fabrication and installation of silt curtain for seawall removal;
•	Maintenance of Silt Curtain and Silt Screens;	•	Maintenance of Silt Curtain and Silt Screens;	•	Maintenance of Silt Curtain and Silt Screens;
•	Sorting of inert C&D material from existing seawall;	•	Sorting of inert C&D material from existing seawall;	•	Sorting of inert C&D material from existing seawall;
•	Disposal of surplus fill material off-site; and	•	Disposal of surplus fill material off-site; and	•	Disposal of surplus fill material off-site; and
•	Reconstruction of New Seawall	•	Reconstruction of New Seawall	•	Reconstruction of New Seawall

2.4.2. Implementation status of the recommended mitigation measures during this reporting period is presented in *Appendix 2.1*.



3. MONITORING REQUIREMENTS

3.1. Noise Monitoring

3.1.1. In accordance with the EIA Report and the approved EM&A Manual, it is anticipated that construction activities, if unmitigated, would not cause any adverse noise impact to the nearest NSRs in the vicinity of the work site. The predicted noise levels at the NSRs would comply with construction noise criteria. These nearest NSRs are designated for construction noise monitoring as listed in *Table 3.1*.

Station Description						
NM1	Planned Residential Development (R3 site)					
NM2	Planned Residential Development (R3 site)					

Table 3.1 Noise Monitoring Stations

3.1.2. As per S.3.1.1 of the approved EM&A Manual states that "Noise levels shall be monitored to evaluate the construction noise impact if there is any planned noise sensitive receivers (NSRs) occupied within 300m from the works area of this Project during the proposed dredging works". Therefore, the impact monitoring for construction noise shall only be carried out when the planned residential development at the two identified monitoring stations are occupied at a later stage.

3.2. Water Quality Monitoring

- 3.2.1. The EIA Report has identified that suspended solids (SS) would be the most critical water quality parameter during the dredging operations. Water quality monitoring for SS and turbidity is therefore recommended to be carried out at selected WSD flushing water intakes. The impact monitoring should be carried out during the proposed dredging works for cruise terminal construction to ensure the compliance with the water quality standards.
- 3.2.2. It is proposed to monitor the water quality at six WSD flushing water intakes along the seafront of the Victoria Harbour. The proposed water quality monitoring stations are shown in *Table 3.2* and *Figure 3.1*.

	Table 5.2 Marine Water Quanty Stations for Water Quanty monitoring								
Station Ref.	WSD Flushing Water Intake	Easting	Northing						
WSD9	Tai Wan	837921.0	818330.0						
WSD10	Cha Kwo Ling	841900.9	817700.1						
WSD15	Sai Wan Ho	841110.4	816450.1						
WSD17	Quarry Bay	839790.3	817032.2						
WSD21	Wan Chai	836220.8	815940.1						
WSD19	Sheung Wan	833415.0	816771.0						

 Table 3.2
 Marine Water Quality Stations for Water Quality Monitoring



WATER QUALITY PARAMETERS AND FREQUENCY

- 3.2.3. During the period of dredging, monitoring should be undertaken three days per week, at midflood and mid-ebb tides, with sampling / measurement at the designated monitoring stations as shown in **Table 3.2**. The interval between two sets of monitoring should not be less than 36 hours except where there are exceedances of Action and/or Limit Levels, in which case the monitoring frequency will be increased. **Table 3.3** shows the proposed monitoring frequency and water quality parameters. Duplicate in-situ measurements and water sampling should be carried out in each sampling event. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should not be less than 0.5m.
- 3.2.4. Silt screens in frame type or floating type shall be deployed at these intakes during the dredging period. It is recommended to conduct the monitoring behind the silt screens at the seawater intake culvert at each seawater pumping station to collect information on the water quality condition after passed the silt screen.

Activities	Monitoring Frequency ¹	Parameters ²	
During the 4-week baseline monitoring period	Three days per week, at mid-flood and mid- ebb tides	Turbidity (in NTU), Suspended Solids (SS in mg/L)	
During dredging works for proposed cruise terminal at Kai Tak	Three days per week, at mid-flood and mid- ebb tides	Turbidity (in NTU), Suspended Solids (SS in mg/L)	

Table 3.3 Water Quality Monitoring Frequency and Parameters

Notes:

- 1. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.
- 2. Turbidity should be measured in situ whereas SS should be determined by laboratory.
- 3.2.5. Supplementary to Baseline Water Quality Monitoring Report Review of Action and Limit Levels (Revision 1.2) was submitted to EPD on 13 October 2011. With respect to the EPD's no comment on the new Action and Limit Levels for water monitoring on 19 October 2011, the new set Action and Limit Levels for turbidity and SS was started to use from 19 October 2011. The established Action and Limit levels can be referred to <u>Appendix 3.1</u>.



4. MONITORING RESULTS

4.1. Water Monitoring Results

- 4.1.1. The water quality monitoring was commenced concurrently with the commencement of dredging works on 28 June 2010. Water quality monitoring was conducted at 6 designated monitoring stations namely WSD9, WSD10, WSD15, WSD17, WSD19 and WSD21 during the reporting quarter.
- 4.1.2. Water monitoring results measured in this reporting period are reviewed and summarized. Details of graphical presentation can be referred in <u>Appendix 4.1.</u> The details of exceedances are summarized in **Table 4.1.1**.

			ws	SD9	ws	D10	ws	D15	ws	D17	ws	D19	ws	D21
			Turb	SS										
Pe	riod	Level	NTU	mg/L										
Mid-flood	Dec-11	AL	0	0	0	0	0	0	0	0	0	0	0	0
	Jan-12		0	0	0	0	0	0	0	0	0	0	0	0
	Feb-12		0	0	0	0	0	1	0	0	0	0	0	0
Mid-ebb	Dec-11	AL	0	0	0	0	0	0	0	0	0	0	0	0
	Jan-12		0	0	0	0	0	0	0	0	0	0	0	0
	Feb-12		0	0	0	0	0	0	0	0	0	0	0	0
Total	of AL Excee	dances:	0	0	0	0	0	1	0	0	0	0	0	0
Mid-flood	Dec-11	LL	0	0	0	0	0	0	0	0	0	0	0	0
	Jan-12		0	0	0	0	0	0	0	0	0	0	0	0
	Feb-12		0	0	0	0	0	0	0	0	0	0	0	0
Mid-ebb	Dec-11	LL	0	0	0	0	0	0	0	0	0	0	0	0
	Jan-12		0	0	0	0	0	0	0	0	0	0	0	0
	Feb-12		0	0	0	0	0	0	0	0	0	0	0	0
Total	Total of LL Exceedances:		0	0	0	0	0	0	0	0	0	0	0	0
T	otal of Excee	dances:	(D	(D		1	()	(0	()

Table 4.1.1 Summary of Exceedances Recorded in the Reporting Quarter

4.1.3. Total 1 SS exceedance was recorded in the reporting period. Investigation found that the exceedance located at the upstream station of the Project site was not due to the Project work. It concluded that no adverse water quality impact was arising from the Project works. Details of investigations can be referred in Section 5.

4.2. Water Quality Surveillance System

- 4.2.1. Six self water quality surveillance monitoring events for removal of existing seawall were conducted in the reporting period. Turbidity and SS monitoring were conducted at 12 locations as follows and shown in *Figure 4.1*.
 - One sampling point inside the silt curtain (SP1);
 - Four sampling points outside the silt curtain (MP1-MP4);
 - Seven control points (C1-C7)



4.2.2. The graphical presentation of the SS levels at SP1, sampling points outside the silt curtain, control points and impact water quality monitoring stations against the distance are shown in *Appendix 4.2*.

4.3. Dredging and Disposal

4.3.1. Implementation of mitigation measures for dredging work and the associated dredging records were checked and the findings are summarized in *Table 4.2.1*.

EP Condition	Compliance Status and/or Recommendation
2.6	In accordance with the EP requirement
Silt Curtain Deployment	
2.6	Complied with the EP requirement in reporting quarter:
and the seabod. Daily Drodging	Maximum daily Dredging Rate was at 890m ³ /day and Maximum hourly Dredging Rate was at 125m ³ /hr.
2.7 Daily Dredging Rate \leq 4,000m ³ /d Hourly Dredging Rate \leq 334m ³ /hr	Complied with the EP requirement in reporting month: Maximum daily Dredging Rate was at 2,273m ³ /day and Maximum hourly Dredging Rate was at 154m ³ /hr.
2.8 Silt Screen Deployment	In accordance with the Silt Screen Deployment Plan for all 6 intakes

 Table 4.2.1 Compliance with EP Conditions in the Reporting Quarter

- 4.3.2. The daily and hourly dredging rates were checked and reviewed that were below the EP requirements. It was concluded that the dredging was conducted in compliance with the specific EP requirements.
- 4.3.3. The dredging and disposal of the sediment (Type 1 Open Sea Disposal (Dedicate Sites) and Type 2 Confined Marine Disposal) to East Sha Chau Contaminated Mud Disposal Site Pit IVc was completed.
- 4.3.4. There were 2,800m³ inert surplus fill materials and 45m³ non-inert C&D material related to dredging works were disposed off site in this reporting quarter.
- 4.3.5. Details of the marine sediment dumping are summarized in *Table 4.2.2*.



Waste Type	Quantity this quarter, m ³ , (Bulk Volume)	Cumulative Quantity- to-Date,m ³ , (Bulk Volume)	Disposal / Dumping Grounds			
Marine Sediment (Type 1 – Open Sea Disposal)	79,431	320,946	South Cheung Chau Spoil Disposal Area denoted "KTCT-1" and "KTCT -2"			
Marine Sediment (Type 1 – Open Sea Disposal (Dedicated Sites) & Type 2 – Confined Marine Disposal) *	NIL	Completed	East Sha Chau Contaminated Mud Disposal Site – Pit IVc			

Table 4.2.2 Waste Quantities Related To Dredging Works

* Remarks: The disposal of marine sediment (Type 1 – Open Sea Disposal (Dedicated Sites) and Type 2 – Confined Marine Disposal) was completed.

8



5. COMPLIANCE AUDIT, REVIEW OF THE REASONS FOR AND THE IMPLICATIONS OF NON-COMPLIANCE

5.0.1. The Event Action Plan for construction noise and water quality is presented in Appendix 5.1.

5.1. Noise Monitoring

5.1.1. Noise monitoring was not necessary in the reporting period.

5.2. Water Quality Monitoring

- 5.2.1. For the suspended solid, the details of exceedance in the reporting period are as follows:
 - 1 Action Level SS exceedances was recorded at WSD15
- 5.2.2. Total 1 SS exceedance was recorded in the reporting period. Silt curtain and silt screens were checked and confirmed in proper condition during the water monitoring. Investigation found that the exceedance was not related to the Project works.
- 5.2.3. For the exceedances, further investigations were conducted to determine the cause of impact in terms of the following areas:
 - Water Quality against the Tidal Movement along Victoria Harbour;
 - Natural Variation Comparison; and
 - Water Quality Surveillance System
- 5.2.4. More details on the investigation are given in Section 5.3 to 5.5.

5.3. Water Quality against the Tidal Movement along Victoria Harbour

- 5.3.1. In order to conclude the cause of an adverse water quality impact, the trend across the 6 monitoring stations is reviewed. Whether the adverse impact is due to project work will be evaluated from the trend of SS level in downstream across the Victoria Harbour after passing the project location. By observing this trend of SS, contribution of the adverse water quality impact from the dredging activities under the project can be evaluated by checking if there is a significant rising up trend in the SS level in the WSD intakes at project downstream.
- 5.3.2. Moreover, a comparison of the monitoring station at project downstream stations with the upstream monitoring stations can also indicate whether the extent of exceedance in SS content recorded at the WSD intakes downstream to the project is likely to be caused by upstream source or not. If the SS values of the upstream and downstream show similar levels, the impact at the project downstream stations shall probably be due to the project upstream streams and the contribution from project work can be eliminated. A review on the tidal movement across the Victoria Harbour is plotted against the SS results against and graphical presentation is presented in <u>Appendix 5.2</u>.
- 5.3.3. Investigations on the recorded upstream exceedances revealed that there were no significant rising up trend of SS levels across the Victoria Harbour after passing the project location. It concluded that no adverse water quality impact was arising from the Project works.



5.4. Natural Variation Comparison

- 5.4.1. Referring to the ER Letter ref. CEDD/KL/2009/01/M45/130(369767) dated 14 February 2011, a Supplementary to Baseline Water Quality Monitoring Report Review Action and Limit Levels (Revision 1.0) has been provided to EPD by ER in February 2011 in according to Sections 4.92 and 10.7 of EM&A Manual. This report in Revision 1.1 has been provided on 26 April 2011 in response to EPD's comments dated 1 April 2011. This report presents the methodology for enlargement baseline database and the review and determination of the Action and Limit Levels in dry and wet seasons.
- 5.4.2. On the basis of this Supplementary to Baseline Water Quality Monitoring Report, the maximum SS levels in the establishment of larger baseline database will be applied and acted as the upper bound of natural variation levels for the comparison with SS results in reporting quarter. The upper bound of natural variation levels are shown in **Table 5.4**. The graphic presentation of water quality results with respect to local variation is shown in **Appendix 5.3**.

Upper Bound of Natural Variation Levels (mg/L)	WSD9	WSD10	WSD15	WSD17	WSD19	WSD21
Dry Season	12.0	19.0	14.0	16.0	18.0	15.0
Wet Season	15.1	21.2	22.7	17.9	17.1	18.8

Table 5.4 Upper Bound of Natural Variation Levels at Water Monitoring Stations

- 5.4.3. According to the graphic presentation, all SS results were well within the upper bound of natural variation levels.
- 5.4.4. Based on the graphic presentation and the trend description of the SS levels in <u>Appendix 4.2</u>, conclusion of the water quality surveillance can be draw as follows:
 - SS level at control point C4 was above trigger level on 10 February 2012, investigations found that there was frequent marine traffic during monitoring and the exceedance was considered non-project related.
 - SS level of MP is lower than SP1 generally;
 - When the WSD intakes were located at upstream of the Project, it found that SS level was occasionally higher than the control points and sampling points near dredging area. Thus, uncertain interference of water quality was apparently interfering in the vicinity of intakes frequently;
- 5.4.5. With reference to the upper bound of natural variation levels and water quality surveillance conducting in reporting period, it shows no fluctuation over the upper bound and hence this further supports such exceedance is not caused by dredging activities.

Summary of Investigation

5.4.6. To summarize, it was found in this reporting period that:



- SS exceedances were located at upstream of the Project site and no rising SS level in downstream across the Victoria Harbour after passing the project location. It definitely concluded that these exceedances were not related to the Project works.
- 5.4.7. Since the investigations found that the exceedance recorded in the reporting quarter was not related to the Project, it was concluded that all necessary steps under Event and Action Plan had been taken. The details of Event and Action Plans and Notification of Exceedance summarizing the finding of investigation, possible causes can be referred to the Monthly EM&A Reports.



5.5. Site Audit

5.5.1. There was no non-compliance from the site audits in the reporting period. During environmental site inspections conducted during the reporting quarter, no particular finding was obtained on the dredging works during the site inspections.

5.6. Summary of action taken in the event of and follow-up on non-compliance

5.6.1. Since the exceedance recorded was not project-related, follow-up mitigation measures were therefore not required.



6. COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION

6.0.1. In the reporting quarter, no complaints, notification of summons or prosecution was received in the reporting period. Cumulative statistic on complaints and successful prosecutions are summarized in *Table 6.1*, *Table 6.2* and *Table 6.3* respectively.

Complaint Log No.		Received From and Received By		Date Investigated	Outcome	Date of Reply
NIL	-	-	-	-	-	-

Table 6.2 Cumulative Statistics on Complaints

Environmental Parameters	Cumulative No. Brought Forward	No. of Complaints This Month	Cumulative No. Project-to-Date
Air	0	0	0
Noise	0	0	0
Water	0	0	0
Waste	0	0	0
Total	0	0	0

Table 6.3 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative No. Project-to-Date
Air	0	0	0
Noise	0	0	0
Water	0	0	0
Waste	0	0	0
Total	0	0	0



7. CONCLUSION

- 7.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.
- 7.0.2. One action level exceedance of SS concentration was recorded in the reporting period. Investigation found that the exceedance was located at the upstream station of the Project site and not due to the Project work. It concluded that no adverse water quality impact was arising from the Project works.
- 7.0.3. Supplementary to Baseline Water Quality Monitoring Report Review of Action and Limit Levels (Revision 1.2) was submitted to EPD on 13 October 2011. With respect to the EPD's no comment on the new Action and Limit Levels for water monitoring on 19 October 2011, the new set Action and Limit Levels for turbidity and SS was started to use from 19 October 2011.
- 7.0.4. Noise monitoring was not necessary in the reporting period.
- 7.0.5. The construction programmes in reporting quarter are provided in <u>Appendix 7.1</u>.



Figure 2.1

General Layout

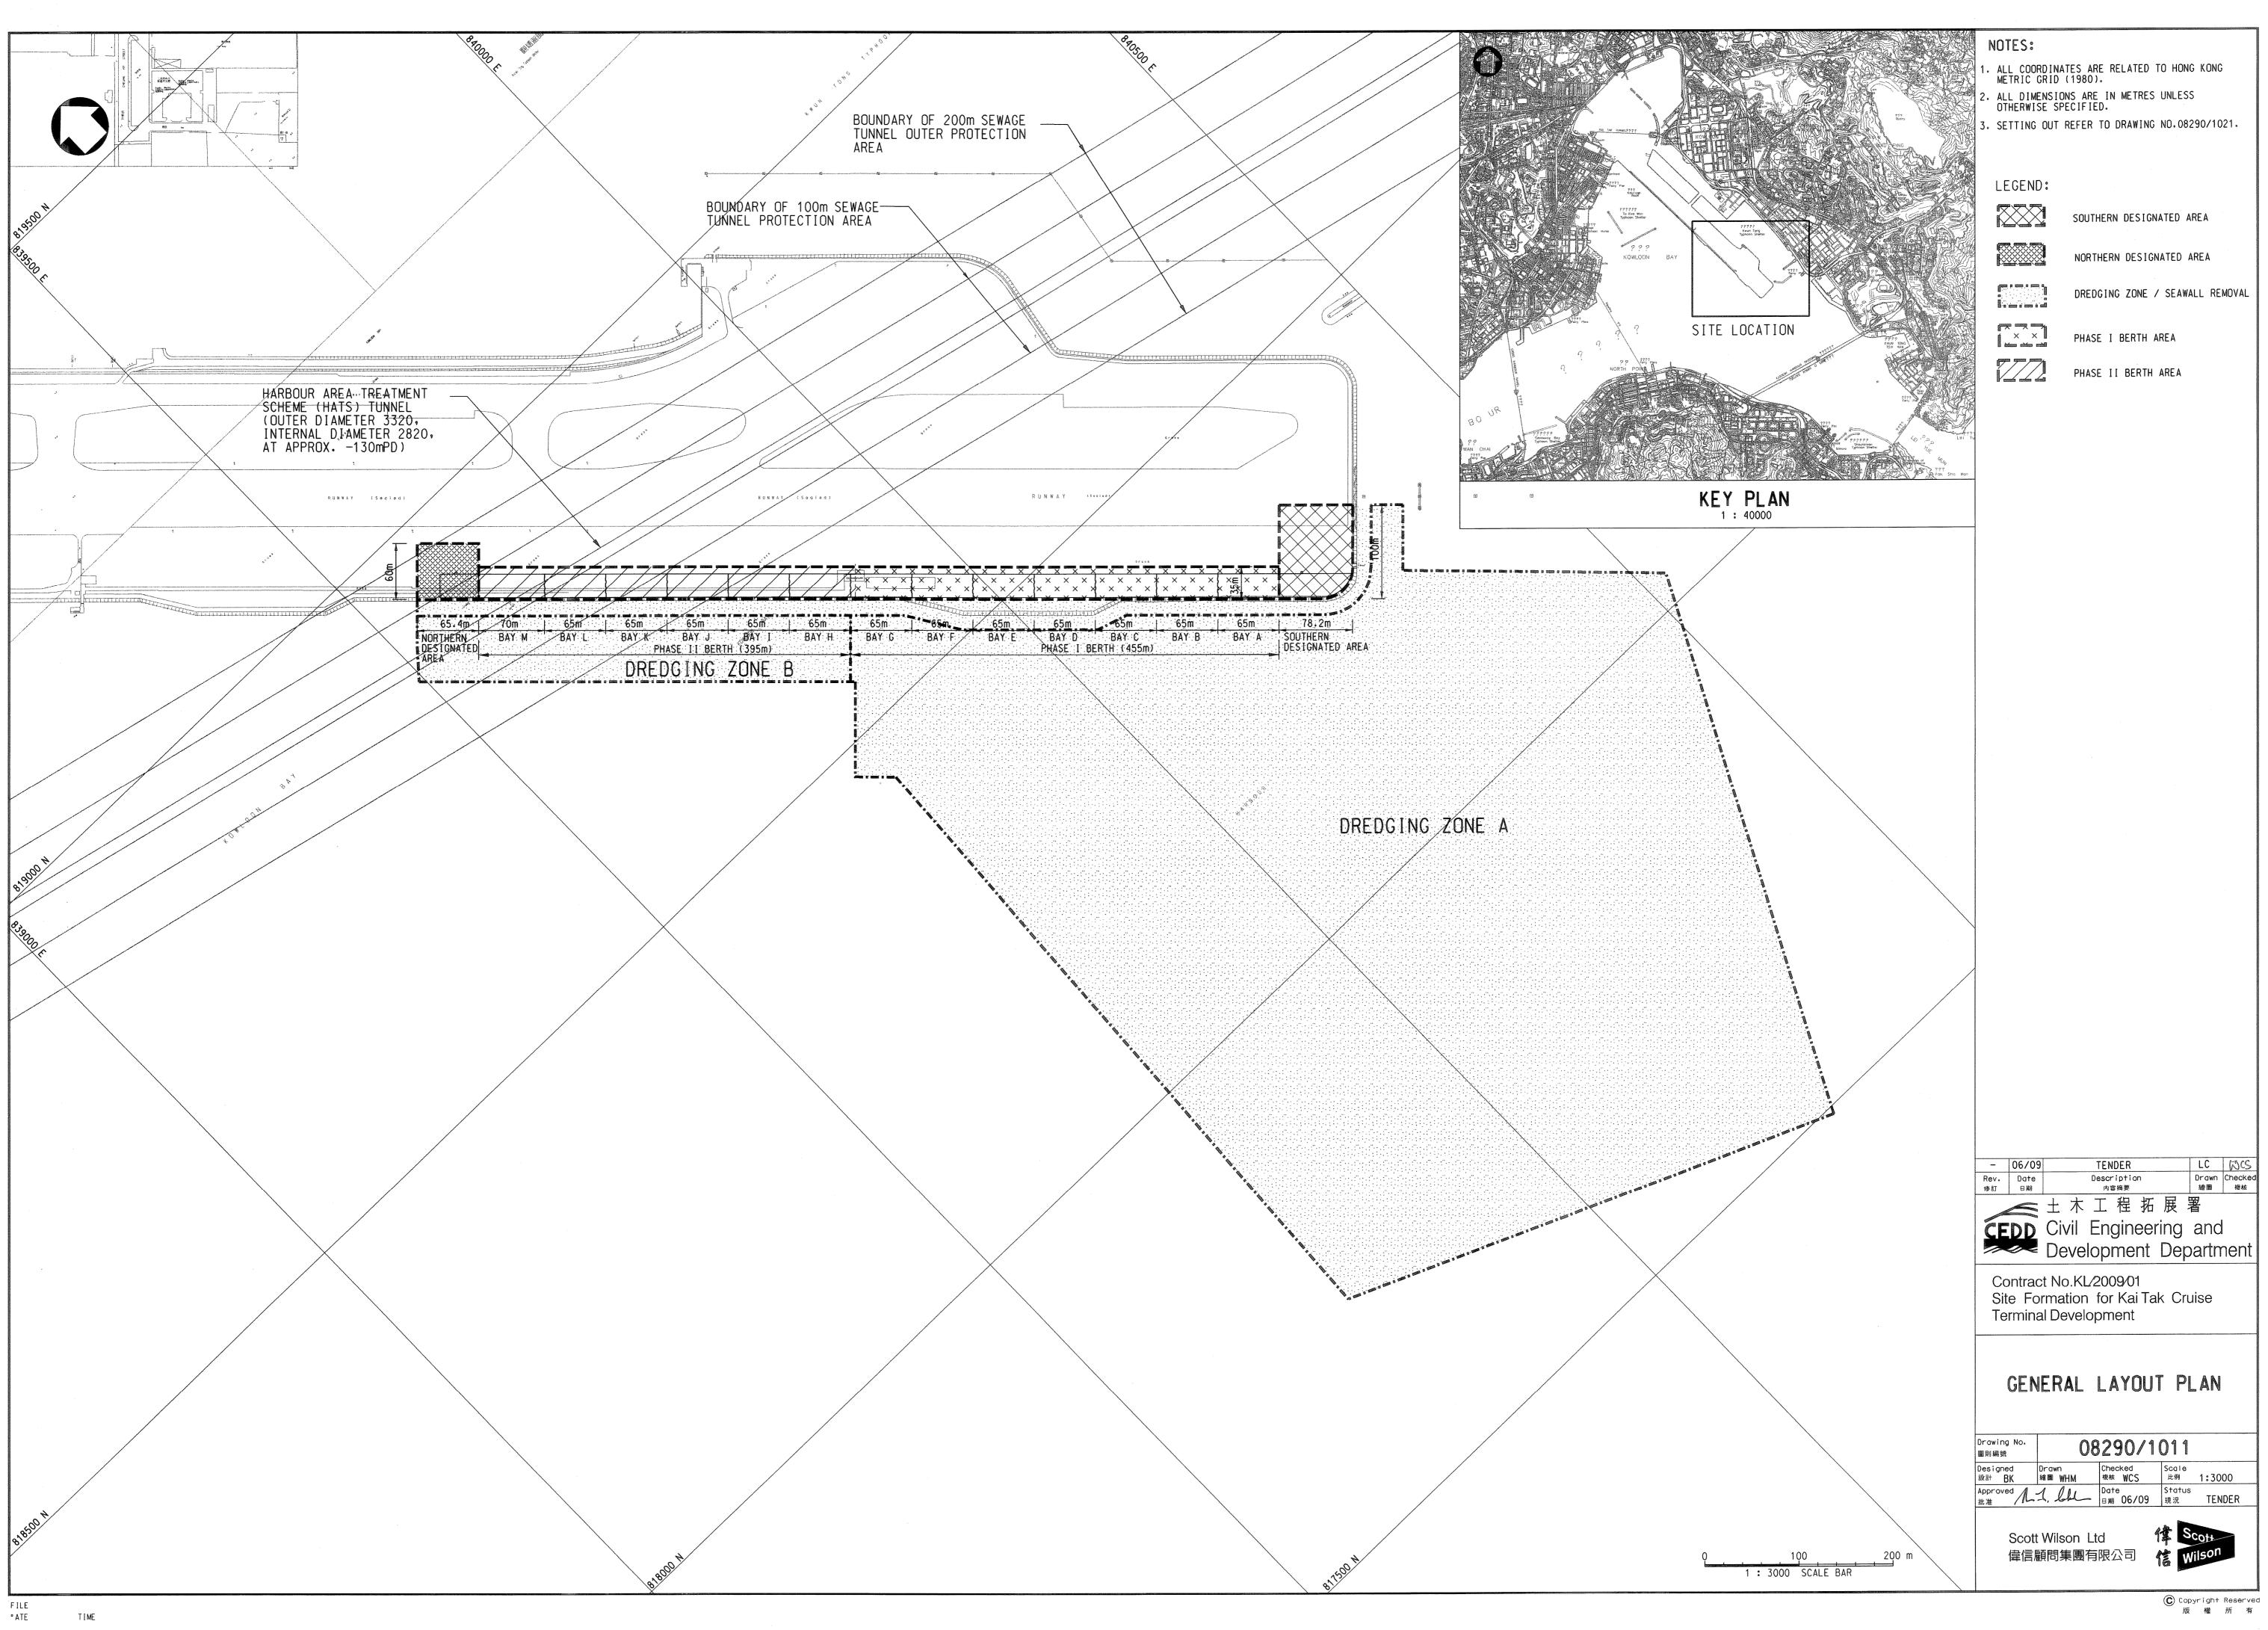




Figure 2.2

Project Organization Chart



Project Organization Chart



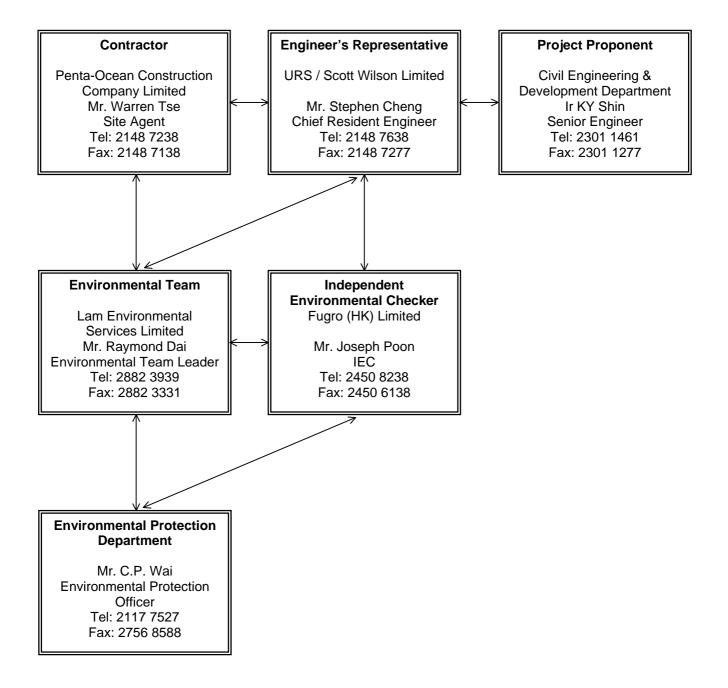




Figure 3.1

Layout of Environmental Monitoring Stations

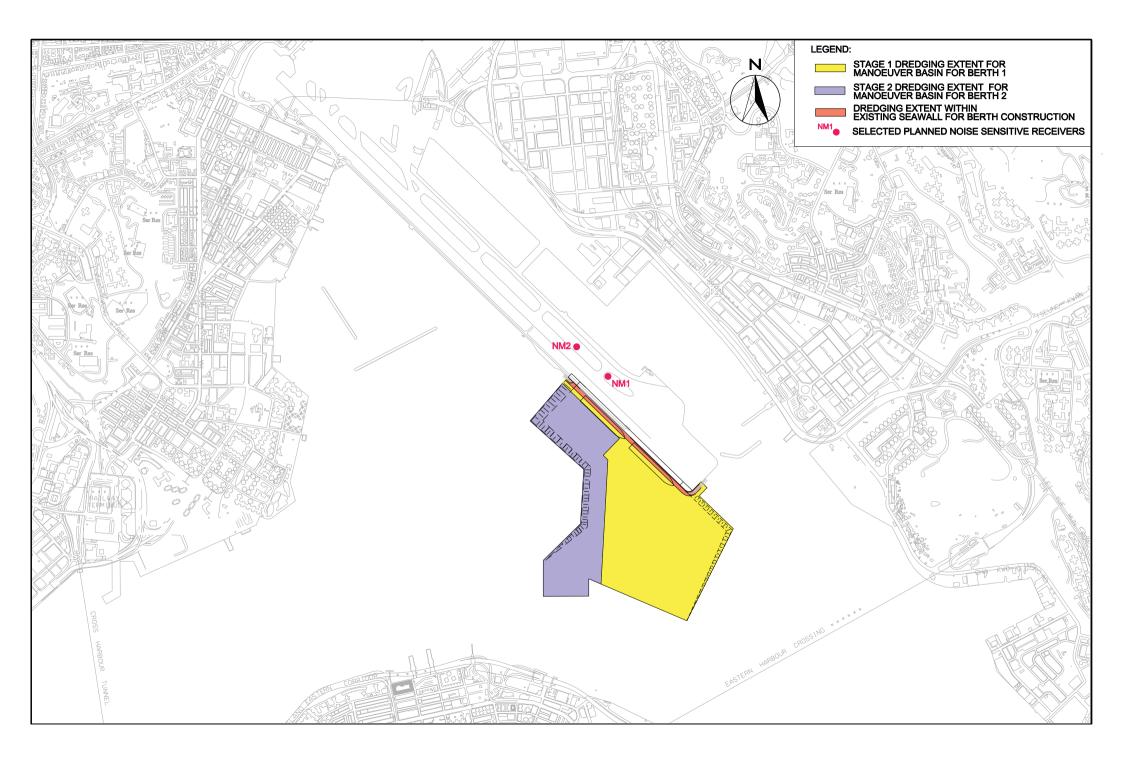

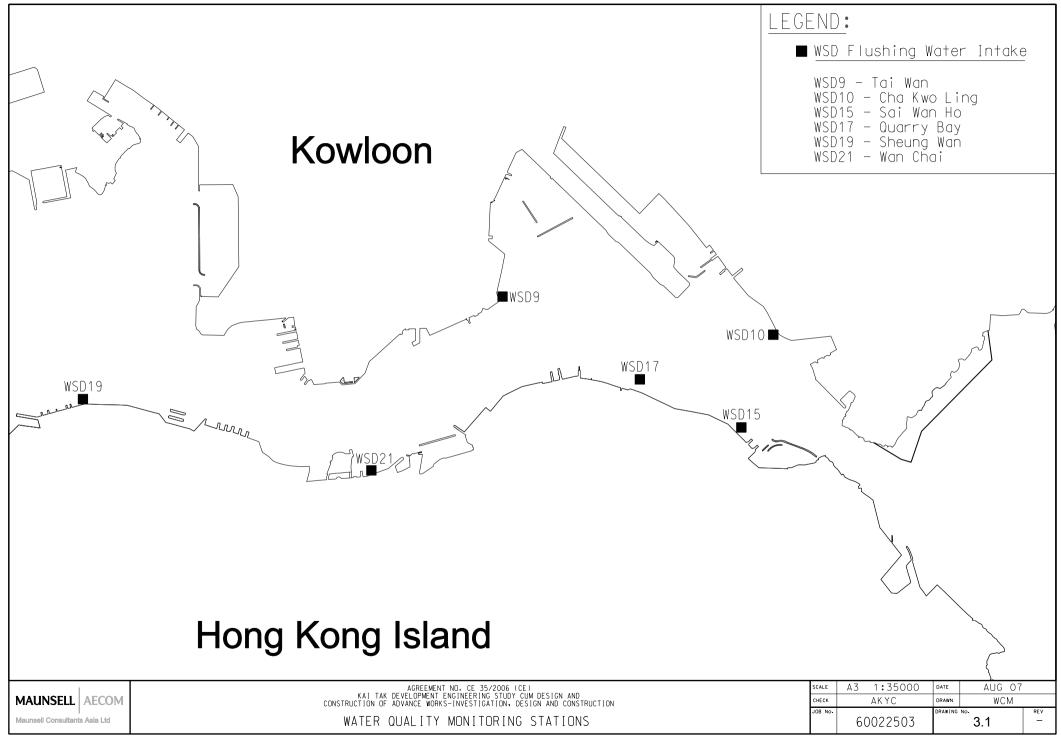


P:/60022503/Reports/CT Dredging/EM&A Manual/Formal submission/Figures/Drawings/4.1.dgn



Figure 4.1

Layout of Monitoring Stations for Water Quality Surveillance System

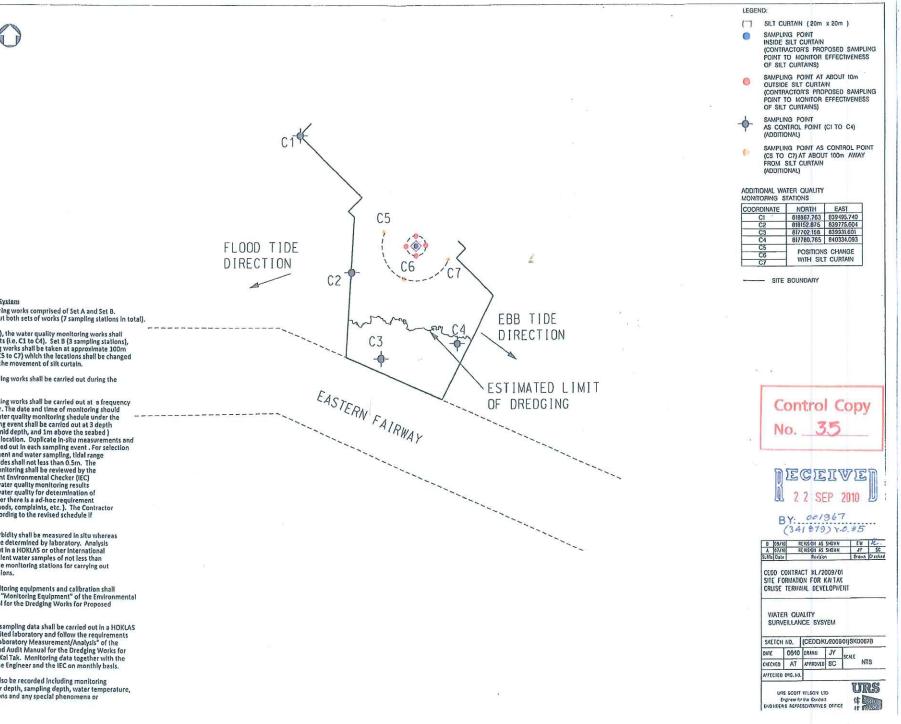

Scope of Works for Water Quality Surveillance System 1. The water quality monitoring works comprised of Set A and Set B. The Contractor shall carry out both sets of works (7 sampling stations in total).

 Set A (4 sampling stations), the water quality monitoring works shall be taken at the Control Points (i.e. C1 to C4). Set B (3 sampling stations), the water quality monitoring works shall be taken at approximate 100m outside the silt curtain (i.e. C5 to C7) which the locations shall be changed from time to time to follow the movement of silt curtain.

3. The water quality monitoring works shall be carried out during the dredging period.


4. The water quality monitoring works shall be carried out at a frequency to be agreed by the Engineer. The date and time of monitoring should be in line with the impact water quality monitoring should under the EM&A manual. Each sampling event shall be carried out at 3 depth (i.e. 1m below the surface, mid depth, and 1m above the seabed) of the water column at each location. Duplicate In-situ measurements and water sampling shall be carried out in each sampling event . For selection Water samping stant be carried out in each samping, event is out of tides for in-situ measurement and water sampling, tidal range of Individual flood and ebb tides shall not less than 0.5m. The schedule of water quality monitoring shall be reviewed by the Engineer and the independent Environmental Checker (IEC) depending on whether the water quality monitoring results could Indicate any trend of water quality for determination of trigger/action level or whether there is a ad-hoc requirement (e.g. change of working methods, complaints, etc.). The Contractor shall carry out the works according to the revised schedule if Instructed by the Engineer.


5. As the key parameters, turbidity shall be measured in situ whereas Suspended Solids (SS) shall be determined by laboratory. Analysis of SS level shall be carried out in a HOKLAS or other international accredited laboratory. Sufficient water samples of not less than 1 liter shall be collected at the monitoring stations for carrying out the laboratory 55 determinations.


6. Requirements on the monitoring equipments and calibration shall be referred to Paragraph 4.7 "Monitoring Equipment" of the Environmental Monitoring and Audit Manual for the Dredging Works for Proposed Cruise Terminal at Kai Tak.


7. Laboratory analysis of the sampling data shall be carried out in a HOKLAS or other international accredited laboratory and follow the requirements as stated in Paragraph 4.8 "Laboratory Measurement/Analysis" of the Environmental Monitoring and Audit Manual for the Dredging Works for Proposed Cruise Terminal at Kal Tak. Monitoring data together with the report shall be reported to the Engineer and the IEC on monthly basis.


8. Other relevant data shall also be recorded including monitoring location/position, time, water depth, sampling depth, water temperature. tidal stages, weather conditions and any special phenomena or work underway nearby.

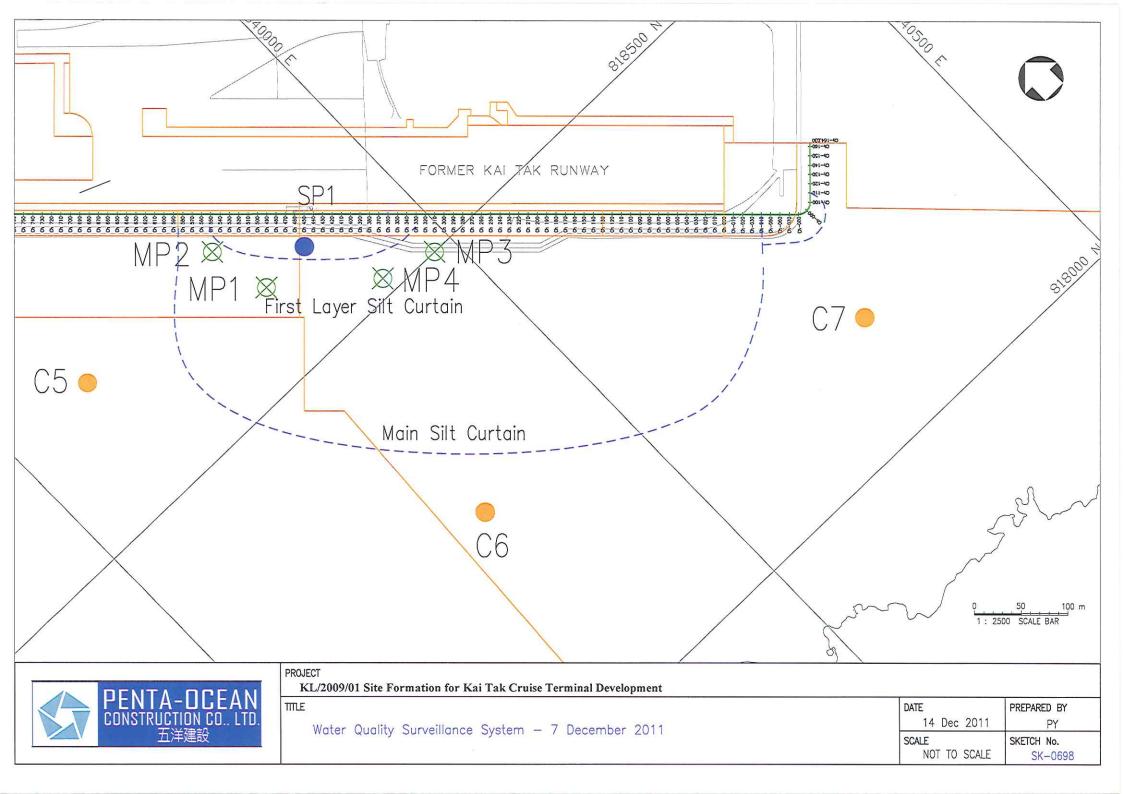


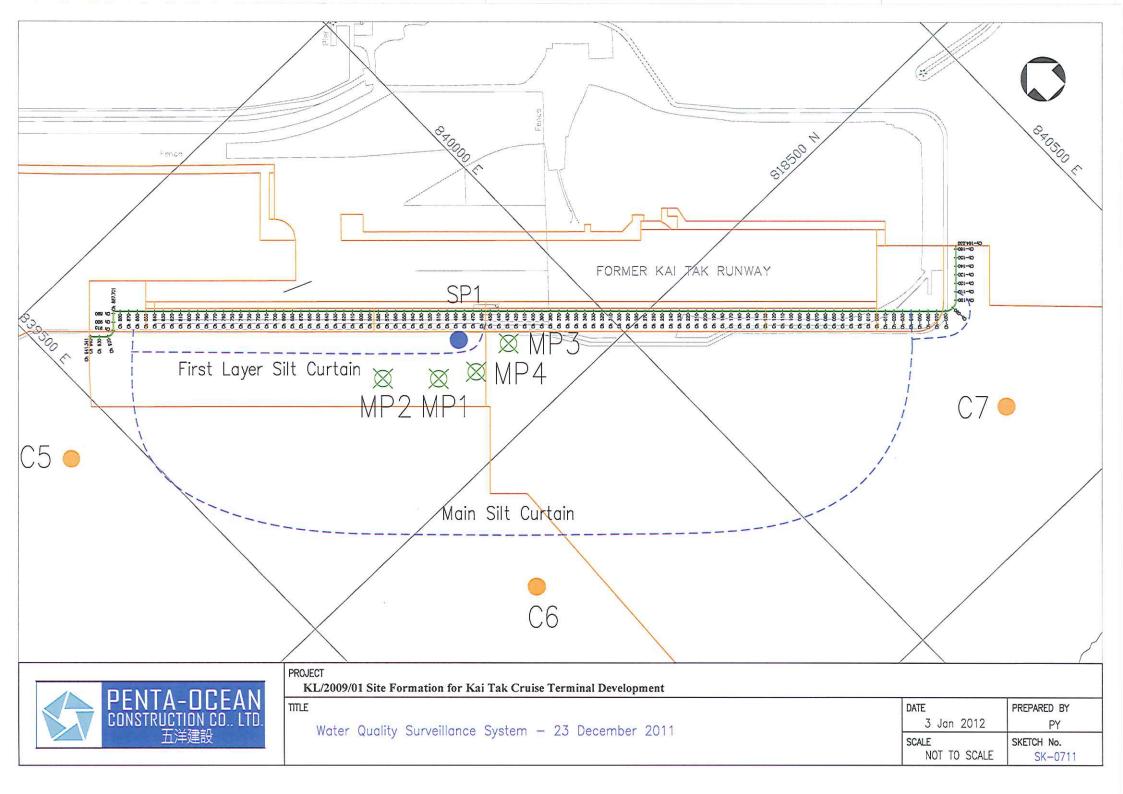

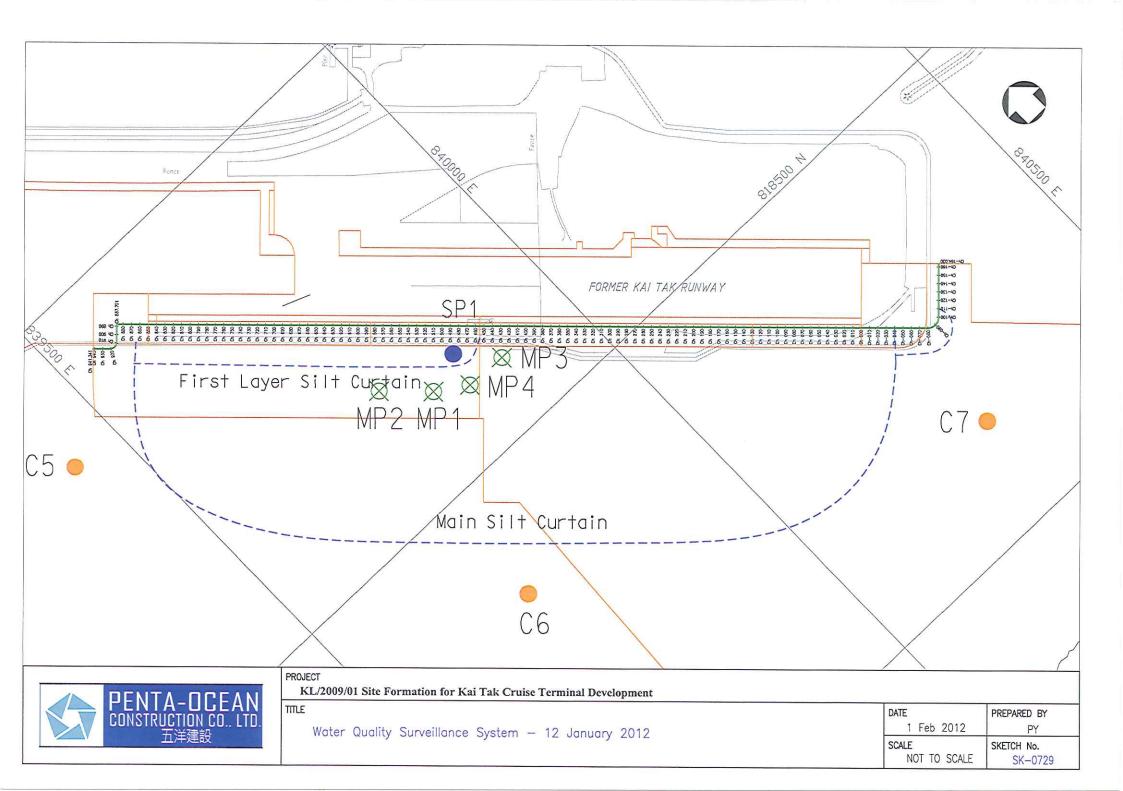

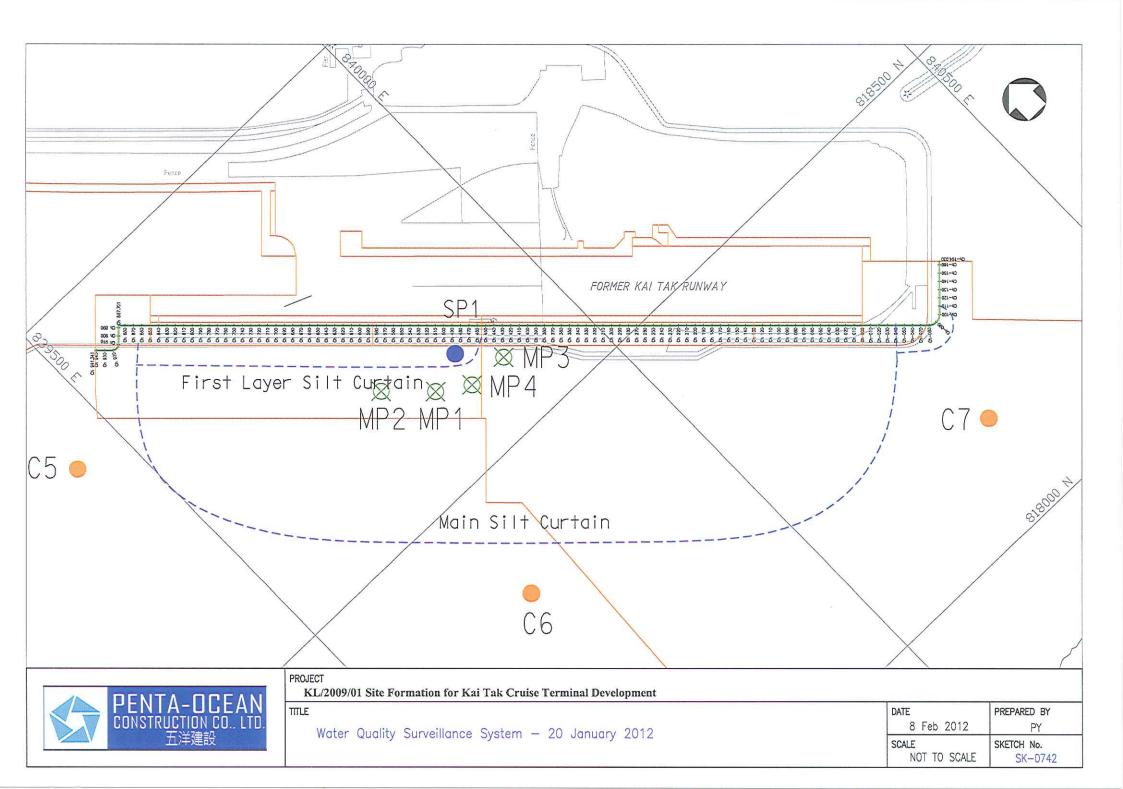

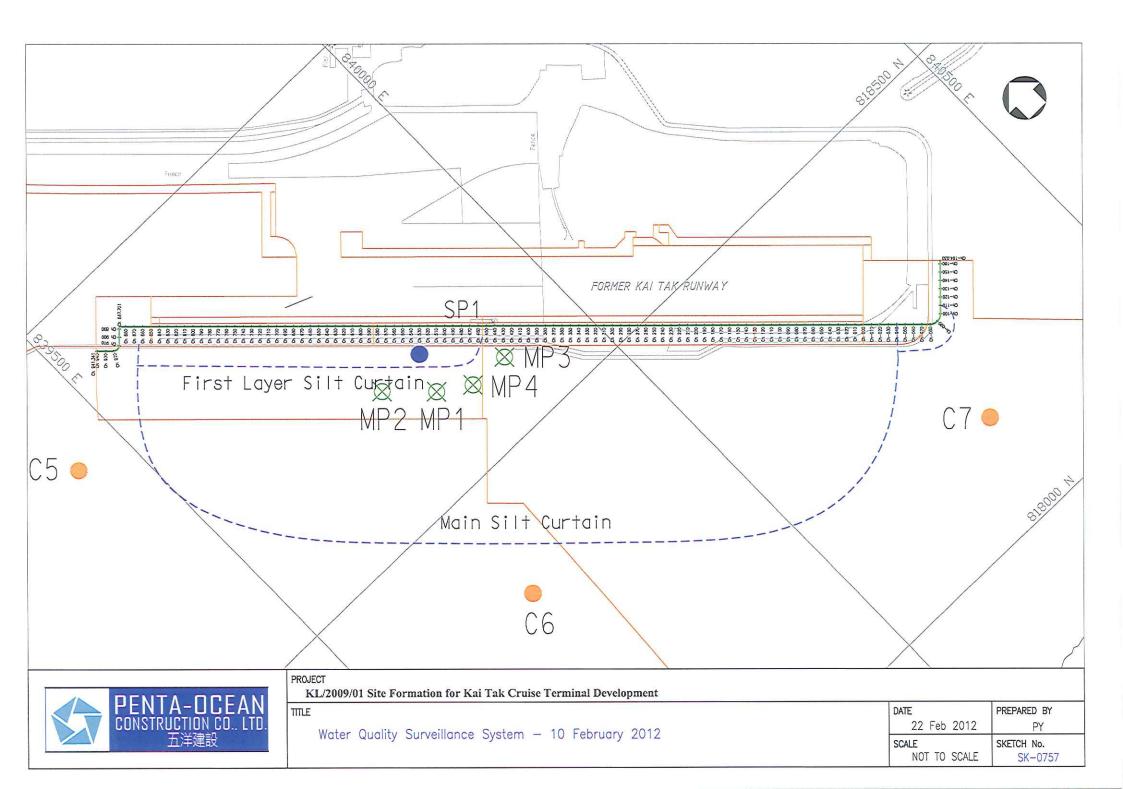

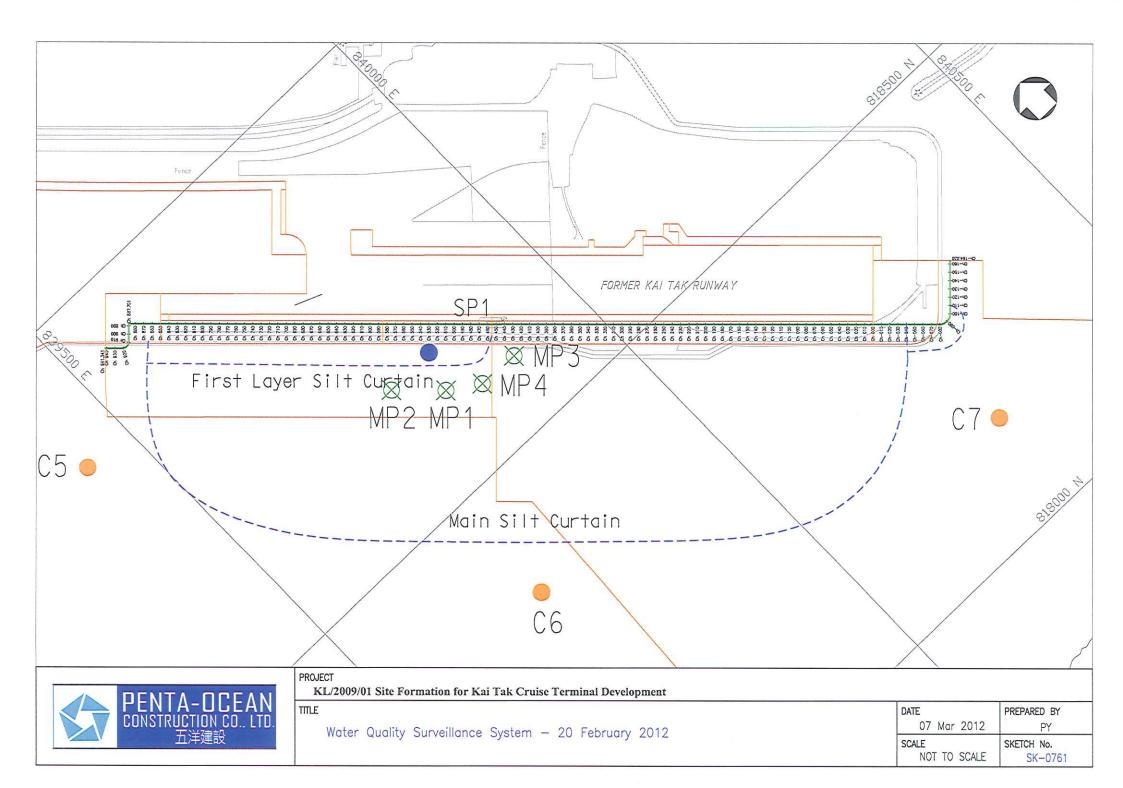



Appendix 2.1

Implementation Schedule of Environmental Mitigation Measures



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S3.6	Requirements of the Air Pollution Control (Construction Dust) Regulation shall be adhered to during the construction period.	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	Air Pollution Control (Construction Dust) Regulation
S3.6	In order to minimize the potential odour emissions, if any, the dredged sediment placed on barge should be properly covered as far as practicable to minimise the exposed area and hence the potential odour emissions during the transportation of the dredged sediment.	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	EIAO-TM
S4.8	 Good Site Practices: Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program. Mobile plant, if any, should be sited as far away from NSRs as possible. Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum. Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	NCO EIAO-TM



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S4.9	If there is any planned NSRs within 300m from the work area occupied during the dredging period, an EM&A programme is recommended to be established according to the predicted occurrence of noisy activities. All the recommended mitigation measures for daytime normal working activities should be incorporated into the EM&A programme for implementation during dredging.	Representative NSRs at the former Kai Tak Airport runway / Upon formal occupation	N/A	Not applicable	NCO EIAO-TM
S5.9	 Dredging will be carried out by closed grab dredger to minimize release of sediment and other contaminants during both capital and maintenance dredging. The maximum production rate for dredging from the seabed to provide necessary manoeuvring area would not be more than 4,000m³ per day (and no more than 2 closed grab dredgers) during capital dredging and 2,000m³ per day (and no more than 1 closed grab dredger) during maintenance dredging. The maximum production rate for dredging at or near the seawall area would not be more than 4,000m³ per day for berth construction. No more than two closed grab dredger would be operated at the same time at or near the seawall for berth construction. 	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	EIAO-TM WPCO
S5.9	Silt curtains should be deployed around the closed grab dredgers used for dredging at and near the existing seawall of the former Kai Tak Airport runway for construction of the cruise berth structures.	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	EIAO-TM, WPCO



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S5.9	Silt screens should be installed at the WSD flushing water intakes at Cha Kwo Ling, Sai Wan Ho, Quarry Bay, Sheung Wan, Wan Chai and Tai Wan for dredging in the manoeuvring basin of the first berth during the capital dredging.	Seawater intakes in Victoria Harbour/ During the construction of cruise terminal	Contractor for capital dredging	Implemented	EIAO-TM, WPCO
S5.9	Silt screens should be installed at the WSD flushing water intakes at Cha Kwo Ling, Quarry Bay and Tai Wan for dredging in the manoeuvring basin of the second berth during the capital dredging.	Seawater intakes in Victoria Harbour / During the construction of cruise terminal	Contractor for capital dredging	Implemented	EIAO-TM, WPCO
S5.9	If the opening has been introduced at the northern runway, silt screens should also be installed at the WSD flushing water intake at Sai Wan Ho, Sheung Wan and Wan Chai for dredging in the manoeuvring basin of the second berth during the capital dredging.	Seawater intake at Sai Wan Ho, Sheung Wan and Wan Chai / During the construction of cruise terminal	Contractor for capital dredging	Implemented	EIAO-TM, WPCO



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S5.9	 Other good site practices that should be undertaken during dredging include: all vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; all barges / dredgers should be fitted with tight fitting seals to their bottom openings to prevent leakage of material; construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site or dumping grounds; barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation. 	Work site and adjacent waters / During dredging in construction stage	Contractor for capital dredging	Implemented	EIAO, EIAO-TM, WPCO, WDO
S5.9	Appropriate numbers of portable chemical toilets shall be provided by a licensed contractor to serve the construction workers over the construction site. The Contractor shall also be responsible for waste disposal and maintenance practices.	Work site and adjacent waters / During dredging in construction stage	Contractor for capital dredging	Implemented	EIAO-TM, WPCO, WDO



Contract No. KL/2009/01 Site Formation for Kai Tak Cruise Terminal Development

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S5.9	Collection and removal of floating refuse should be performed at regular intervals on a daily basis. The contractor should be responsible for keeping the water within the site boundary and the neighbouring water free from rubbish during the dredging works.	Work site and adjacent waters / During dredging in construction stage	Contractor for capital dredging	Implemented	EIAO-TM, WPCO, WDO
S5.9	An environmental monitoring and audit programme should be implemented to verify whether or not impact predictions are representative, and to ensure that all the recommended mitigation measures are implemented properly. If the water quality monitoring data indicate that the proposed dredging works result in unacceptable water quality impacts in the receiving water, appropriate actions should be taken to review the dredging operation and additional measures such as use of frame-type silt curtain, deployment of double silt curtains, slowing down, or rescheduling of works should be implemented as necessary.	6 selected WSD flushing water intakes in Victoria Harbour/ During dredging in construction stage	Environmental Team and verified by Independent Environmental Checker	Implemented	EIAO-TM, WPCO



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S5.9	Silt screens are recommended to be deployed at 6 selected WSD flushing water intakes during the capital dredging. The contractor for capital dredging shall demonstrate and ensure that the design of the silt screen will not affect the normal operation of flushing water intake. The contractor shall obtain consensus from all relevant parties, including WSD and Marine Department on the design of the silt screen at each of the six selected flushing water intake points before installation of the silt screen and commencement of the proposed dredging works. As a mitigation measure to avoid the pollutant and refuse entrapment problems and to ensure that the impact monitoring results are representative, regular maintenance of the silt screens and refuse collection should be performed at the monitoring stations at regular intervals on a daily basis. The Contractor should be responsible for keeping the water behind the silt screen free from floating rubbish and debris during the impact monitoring period.	6 selected WSD flushing water intakes in Victoria Harbour/ During dredging in construction stage	Contractor for capital dredging	Implemented	EIAO-TM, WPCO



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines				
S6.7	Good Site Practices It is not anticipated that adverse waste management related impacts would arise, provided that good site practices are adhered to. Recommendations for good site practices during the dredging activities include:	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	EIAO-TM				
	• Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.								
	• Training of site personnel in proper waste management and chemical waste handling procedures.								
	• Provision of sufficient waste disposal points and regular collection for disposal.								
	• Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.								
	• A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).								
	• Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.								



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S6.7 (cont.)	 Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the workforce. Any unused chemicals or those with remaining functional capacity shall be recycled. 	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	EIAO-TM
S6.7	Marine Sediments The dredged marine sediments would be loaded onto barges and transported to the designated disposal sites allocated by the MFC depending on their level of contamination. Sediment classified as Category L would be suitable for Type 1 – Open Sea Disposal. Contaminated sediment would require either Type 1 – Open Sea Disposal (Dedicated Sites) or Type 2 - Confined Marine Disposal and must be dredged and transported with great care in accordance with ETWB TCW No. 34/2002. Subject to the final allocation of the disposal sites by MFC, the dredged contaminated sediment must be effectively isolated from the environment upon final disposal and shall be disposed of at the East Sha Chau Contaminated Mud Pits that are designated for the disposal of contaminated mud in Hong Kong.	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	ETWB TCW No. 34/2002



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S6.7	It will be the responsibility of the Contractor to satisfy the appropriate authorities that the contamination levels of the marine sediment to be dredged have been analysed and recorded. According to the ETWB TCW No. 34/2002, this will involve the submission of a formal Sediment Quality Report to the DEP, prior to the dredging contract being tendered. The contractor for the dredging works shall apply for the allocation of marine sediment disposal sites from all relevant authorities.	Work site / During dredging in construction stage	Contractor for capital dredging	Dumping Permits were issued by EPD	ETWB TCW No. 34/2002
S6.7	 During transportation and disposal of the dredged marine sediments requiring Type 1 and Type 2 disposal, the following measures shall be taken to minimise potential impacts on water quality: Bottom opening of barges shall be fitted with tight fitting seals to prevent leakage of material. Excess material shall be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved. Monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the DEP. Barges or hopper barges shall not be filled to a level that would cause the overflow of materials or sediment laden water during loading or transportation. 	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	WDO; WPCO



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S6.7	Chemical Wastes After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals should be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
S6.7	General Refuse General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material.	Work site / During dredging in construction stage	Contractor for capital dredging	Implemented	WDO, WPCO



EIA Ref [#]	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S6.7	Construction and Demolition Material It is recommended that the extent of dredging of the existing seawall should be kept to a minimum in the detailed design of the new cruise terminal to minimize generation of C&D material. Mitigation measures and good site practices should be incorporated in the contract document to control potential environmental impact from handling and transportation of C&D material. The mitigation measures include: • Where it is unavoidable to have transient stockpiles of C&D material within the Project work site pending collection for disposal, the transient stockpiles shall be located away from waterfront or storm drains as far as possible. • Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric. • Skip hoist for material transport should be totally enclosed by impervious sheeting. • Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site.	Work site / During the construction period	Contractor for capital dredging	Implemented	ETWB TCW No. 33/2002, 31/2004, 19/2005
	• The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.				



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S6.7 (cont.)	 The load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle. All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet. The height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading. 	Work site / During the construction period	Contractor for capital dredging	Implemented	ETWB TCW No. 33/2002, 31/2004, 19/2005
S6.7	When delivering inert C&D material to public fill reception facilities, the material shall consist entirely of inert construction waste and of size less than 250mm or other sizes as agreed with the Secretary of the Public Fill Committee. In order to monitor the disposal of the surplus C&D material at the designed public fill reception facility and to control fly tipping, a trip-ticket system should be included as one of the contractual requirements and implemented by the Contractor under the Waste Management Plan certified by the Environmental Team and verified by the Independent Environmental Checker who should be responsible for auditing the results of the system.	Work site / During the construction period	Contractor for capital dredging, Engineer, Environmental Team and Independent Environmental Checker	Not applicable	ETWB TCW No. 31/2004



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S7.8	The dredging activities of the proposed cruise terminal should ensure that disturbance to the existing seawall masonry outside the Project boundary should be avoided as far as practicable.	Work site/ During construction of cruise terminal	Contractor for capital dredging as per CEDD's advice	Implemented	Antiquities and Monuments Ordinance EIAO, EIAO-TM Guidance Notes on Assessment of Impact on Sites of Cultural Heritage in Environmental Impact Assessment Studies (GN-CH) Hong Kong Planning Standards and Guidelines (HKPSG)
S7.10, App. 7.1	It is recommended that the dredged spoil should be monitored for the presence of archaeological material. Guidelines for the monitoring brief have been prepared in consultation with the AMO. A qualified marine archaeologist needs to be on standby to provide specialist advice, if required, but the monitoring can be carried out by a member of staff on the dredging barge.	Work site / during dredging in construction stage	Contractor for capital dredging, Environmental Team	Implemented	Antiquities and Monuments Ordinance EIAO, EIAO-TM GN-CH HKPSG Marine Archaeological Investigation Guidelines



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
8.7	Translocate those existing coral colonies attached on boulders that are manually movable by a diver underwater (possibly longest dimension of less than 50cm) located within the hard substrata sea area within the dredging site as far as practicable prior to the commencement of the capital dredging activities. The entire translocation exercise include the preparation of a detailed translocation plan, the pre- translocation coral survey, the coral translocation, and the quarterly post-translocation monitoring for one year. Pre-translocation survey would be focused on identifying and mapping of coral colonies that would be directly impacted by the proposed dredging and investigating the translocation feasibility of these coral colonies. A detailed translocation plan (including pre- translocation coral survey, translocation methodology and monitoring of transplanted corals) should be prepared during the detailed design stage of the Project which, together with the ecologist involved in coral translocation, should be approved by AFCD prior to commencement of the translocation exercises. The proposed relocation of the coral colonies should not affect any private/public marine rights at the recipient site.	Along the section of the former Kai Tak Airport runway that will be directed affected by the cruise terminal construction / During detailed design stage	Other ET specifically employed for coral translocation works	Final Detailed Coral Translocation Plan was approved by EPD in letter ref. (18) in EP2/K19/C/19 Pt.5 dated 5 June 2009. Form 5 was submitted under CEDD's memo ref. (6) in KD 2/31/4 Pt.3 dated 10 June 2009 regarding minor alteration of the position of the coral recipient site. Coral Translocation Report was submitted in Scott Wilson letter ref. 08290/325723 dated 2 July 2009. Post-translocation report shall be referred to the submissions by another ET specifically employed for coral translocation works.	EIAO-TM



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Status	Relevant Legislation and Guidelines
S8.7	New seawalls at the berth structure of the cruise terminal shall be constructed in order to provide large area of hard substrata for settlement and recruitment of intertidal and subtidal assemblages similar to those previously recorded from existing habitats.	The section of the former Kai Tak Airport runway that will be directed affected by the cruise terminal construction / During detailed design stage	To be confirmed at later stage	To be confirmed at later stage	EIAO-TM
9.6	No fisheries-specific mitigation measures would be required.	-	Not applicable	Not applicable	-



Appendix 3.1

Action and Limit Levels



Action and Limit Levels

Action and Limit Levels for Noise Monitoring

Time Period	Action Level	Limit Level
07:00 – 19:00 hours on normal weekdays	When one documented complaint is received from any one of the sensitive receivers	75 dB(A)

Remarks: No noise monitoring was conducted due to no planned noise sensitive receivers (NSRs) occupied within 300m from the works area of this Project during the dredging works.

Action and Limit Levels for Water Monitoring

Parameters	Action L	evel		Limit Le	vel	
Turbidity in NTU		All Sease	on		All Sease	<u>on</u>
	WSD9	5.67		WSD9	12.27	
	WSD10	6.26	;	WSD10	10.47	
	WSD15	8.15	i	WSD15	14.41	
	WSD17	11.60	1	WSD17	16.91	
	WSD21	9.11		WSD21	15.38	i i
	WSD19	13.09	I	WSD19	15.34	
Suspended Solids		Dry Season	Wet Season		<u>Dry Season</u>	Wet Season
(SS) in mg/L	WSD9	6.9	9.7	WSD9	7.8	10.9
	WSD10	7.7	9.1	WSD10	10.3	12.2
	WSD15	7.8	13.5	WSD15	8.4	14.5
	WSD17	9.5	11.2	WSD17	13.7	16.2
	WSD21	13.3	17.1	WSD21	13.9	17.8
	WSD19	16.3	15.1	WSD19	17.0	15.7

Remarks:

Wet season is the period from April to September.

Dry season is the period from October to March.

Revised Action and Limit Levels for Water Monitoring

Station	Turbidity (NTU)				Suspended Solid (mg/L)			
	Action Level for Limit Level individual stations					Limit Level for individual stations		
	Dry Season	Wet Season	Dry Season	Wet Season	Dry Season	Wet Season	Dry Season	Wet Season
WSD9	5.6	7.0	10.6	13.4	10.2	12.8	10.8	13.5
WSD10	6.3	8.1	9.4	12.1	10.0	11.2	11.8	13.2
WSD15	7.5	11.9	12.5	19.6	10.8	17.5	11.8	19.1



Station	Turbidity (N	NTU)			Suspended Solid (mg/L)			
	Action Level for Limit Level individual stations					Limit Level for individual stations		
	Dry Season	Wet Season	Dry Season	Wet Season	Dry Season	Wet Season	Dry Season	Wet Season
WSD17	10.0	12.9	15.3	19.7	13.2	14.7	15.3	17.0
WSD19	10.9	13.7	14.7	18.4	14.0	13.3	17.0	16.2
WSD21	8.9	11.6	13.4	17.6	13.3	16.7	14.0	17.5

Revised Action and Limit Levels for water monitoring was approved on 19 October 2011.





Appendix 4.1

Graphical Presentation of Water Quality Monitoring Results



Graphic Presentation of Water Quality Result of WSD9 - Tai Wan

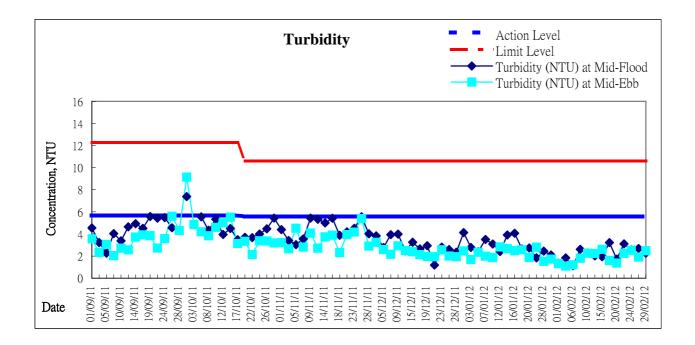

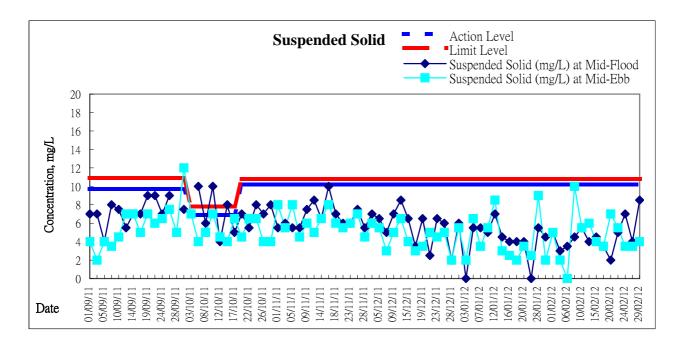

Remarks:


- Two sets of Suspended Solid Action and Limit levels for the dry season (the period from October to March)


and wet season (the period from April to September).

- New sets Turbidity and SS Action Level and Limit Level for dry and wet season were approved by EPD on 19 Oct 2011



Graphic Presentation of Water Quality Result of WSD10 - Cha Kwo Ling

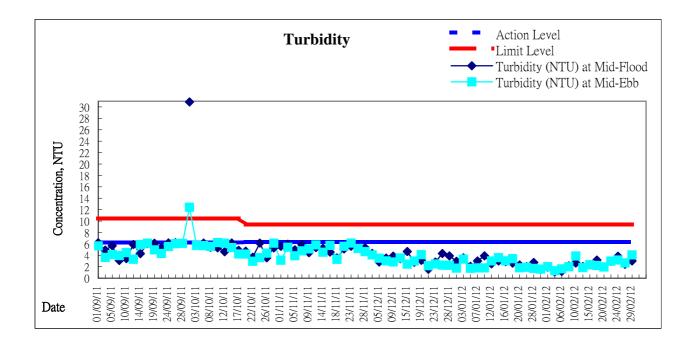

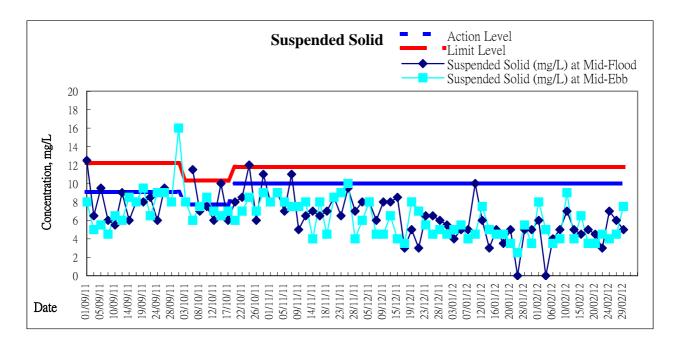


- Two sets of Suspended Solid Action and Limit levels for the dry season (the period from October to March)


and wet season (the period from April to September).

- New sets Turbidity and SS Action Level and Limit Level for dry and wet season were approved by EPD on 10 Oct 2011



Graphic Presentation of Water Quality Result of WSD15 - Sai Wan Ho

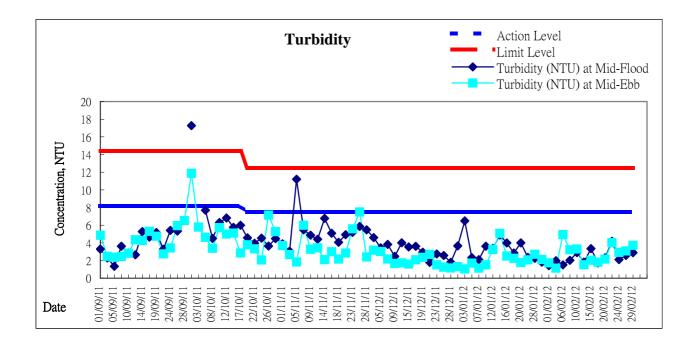

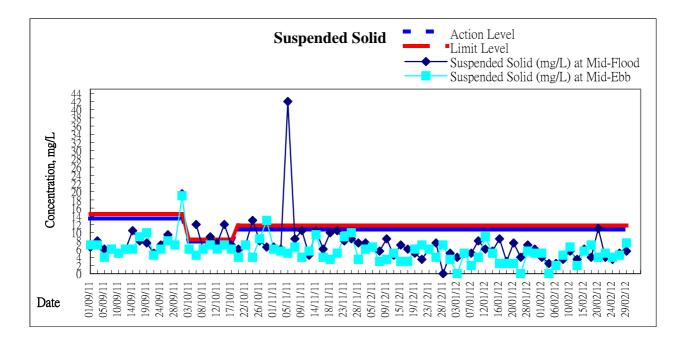


- Two sets of Suspended Solid Action and Limit levels for the dry season (the period from October to March)


and wet season (the period from April to September).

- New sets Turbidity and SS Action Level and Limit Level for dry and wet season were approved by EPD



Graphic Presentation of Water Quality Result of WSD17 - Quarry Bay

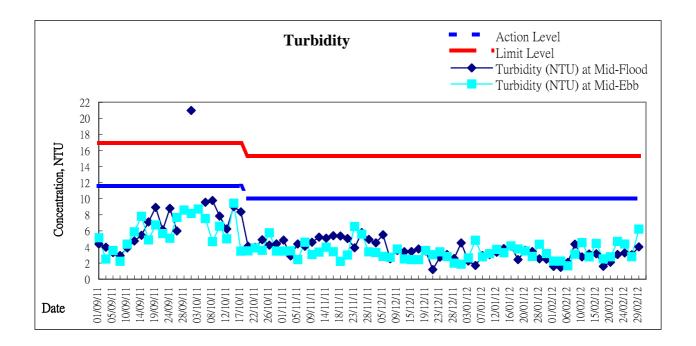

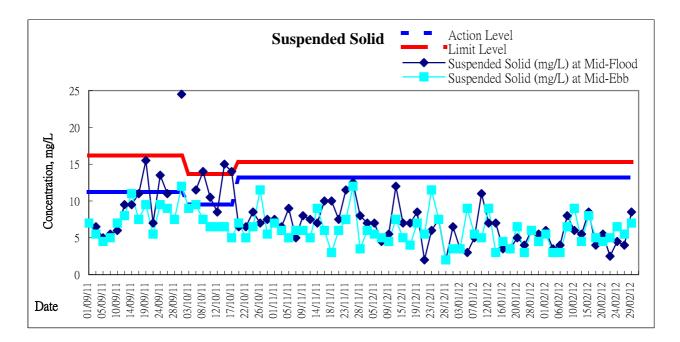


- Two sets of Suspended Solid Action and Limit levels for the dry season (the period from October to March)


and wet season (the period from April to September).

- New sets Turbidity and SS Action Level and Limit Level for dry and wet season were approved by EPD on 10 Oct 2011



Graphic Presentation of Water Quality Result of WSD19 - Sheung Wan

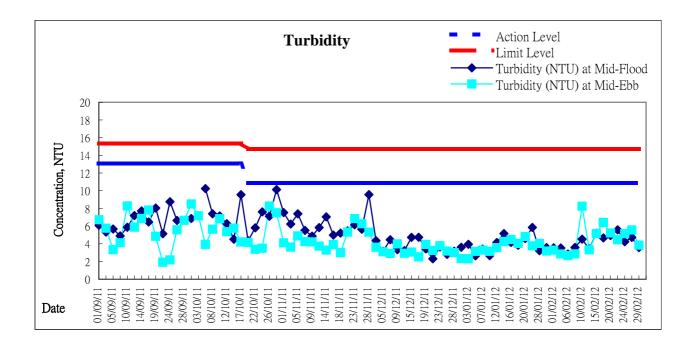

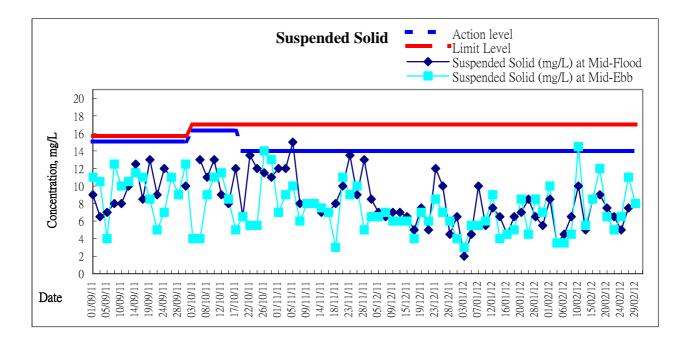



- Two sets of Suspended Solid Action and Limit levels for the dry season (the period from October to March)

and wet season (the period from April to September).

- New sets Turbidity and SS Action Level and Limit Level for dry and wet season were approved by EPD on 19 Oct 2011



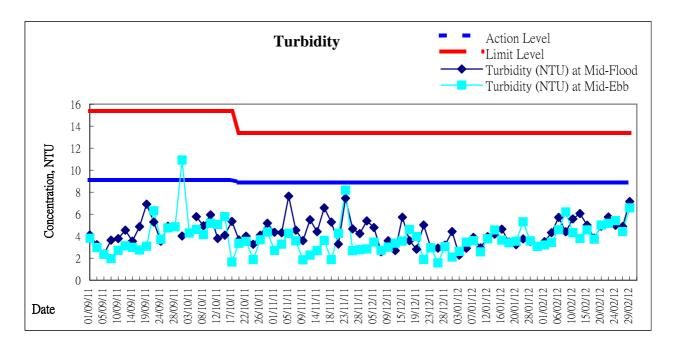

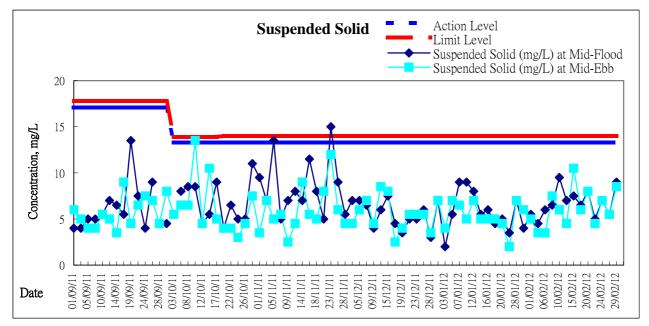

- Two sets of Suspended Solid Action and Limit levels for the dry season (the period from October to March)

and wet season (the period from April to September).

- New sets Turbidity and SS Action Level and Limit Level for dry and wet season were approved by EPD on 19 Oct 2011




Appendix 4.2


Graphical Presentation of Water Quality Surveillance


Water Quality Surveillance System Monitoring Results - 7 December 2011 (Ebb Tide)

Monitoring Location		Turbidity in	Compare to	Suspended	Compare to
		NTU	Trigger Level	Solids in mg/L	Trigger Level
		5.75	N/A	13	N/A
SP1	mid depth	6.29	N/A	13	N/A
	1m above the seabed	4.19	N/A	8	N/A
	1m below the surface	2.71	N/A	6	N/A
MP1	mid depth	2.56	N/A	3	N/A
	1m above the seabed	3.02	N/A	6	N/A
	1m below the surface	2.78	N/A	4	N/A
MP2	mid depth	2.52	N/A	8	N/A
	1m above the seabed	3.22	N/A	4	N/A
	1m below the surface	3.36	N/A	7	N/A
MP3	mid depth	2.56	N/A	5	N/A
	1m above the seabed	2.56	N/A	6	N/A
	1m below the surface	2.53	N/A	6	N/A
MP4	mid depth	2.36	N/A	3	N/A
	1m above the seabed	2.54	N/A	10	N/A
	1m below the surface	3.28	Lower	4	Lower
C1	mid depth	2.28	Lower	7	Lower
	1m above the seabed	2.34	Lower	5	Lower
	1m below the surface	2.39	Lower	14	Equal
C2	mid depth	2.50	Lower	5	Lower
	1m above the seabed	2.37	Lower	5	Lower
	1m below the surface	2.26	Lower	3	Lower
C3	mid depth	2.41	Lower	5	Lower
	1m above the seabed	2.08	Lower	4	Lower
	1m below the surface	2.73	Lower	4	Lower
C4	mid depth	2.42	Lower	8	Lower
	1m above the seabed	2.79	Lower	4	Lower
	1m below the surface	2.56	N/A	6	N/A
C5	mid depth	2.22	N/A	4	N/A
	1m above the seabed	2.22	N/A	8	N/A
	1m below the surface	2.22	N/A	5	N/A
C6	mid depth	2.21	N/A	4	N/A
00	1m above the seabed	2.64	N/A	4	
	1m below the surface	2.39	N/A	6	N/A
C7	mid depth	6.29	N/A	14	N/A
07	1m above the seabed	3.77	N/A	6	N/A

Control Point	Trigger Level for Turbidity in NTU for All Season	Trigger Level for SS in mg/L for Dry Season (October - March)
C1	12.3 for Flood Tide	
C2	12.3 for Flood Tide	14.0
C3	16.9	14.0
C4	10.5 for Ebb Tide	

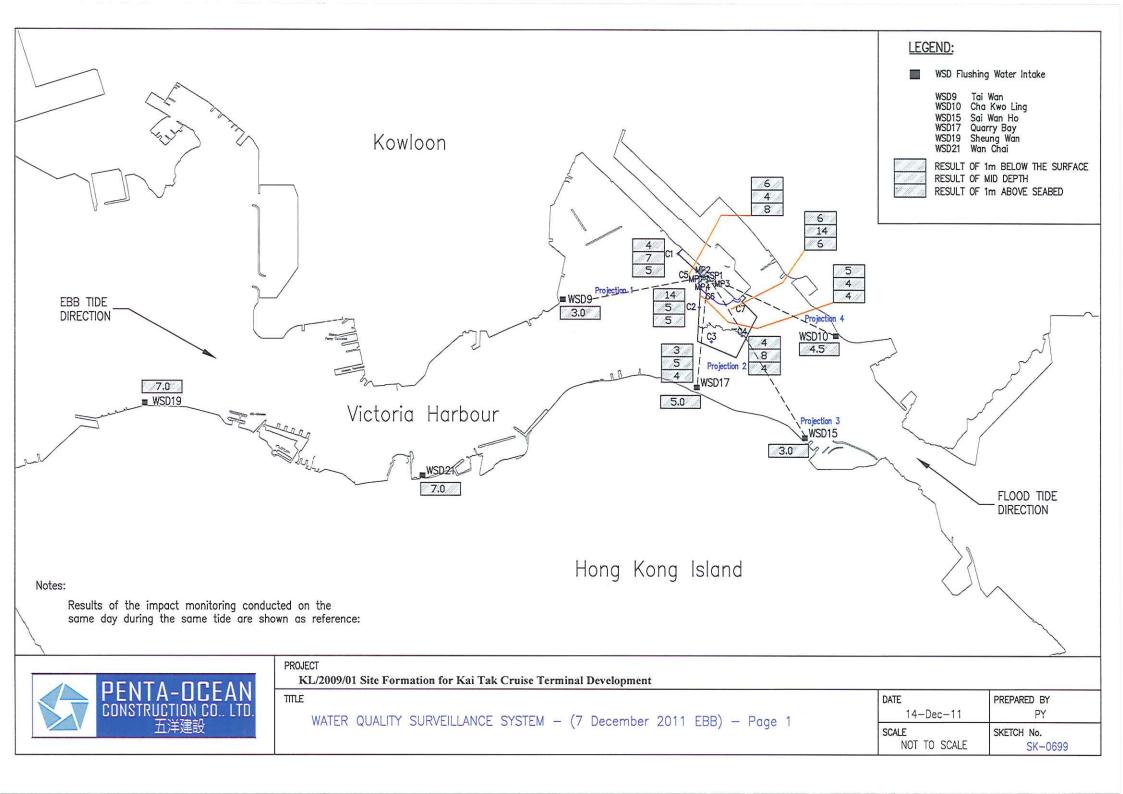

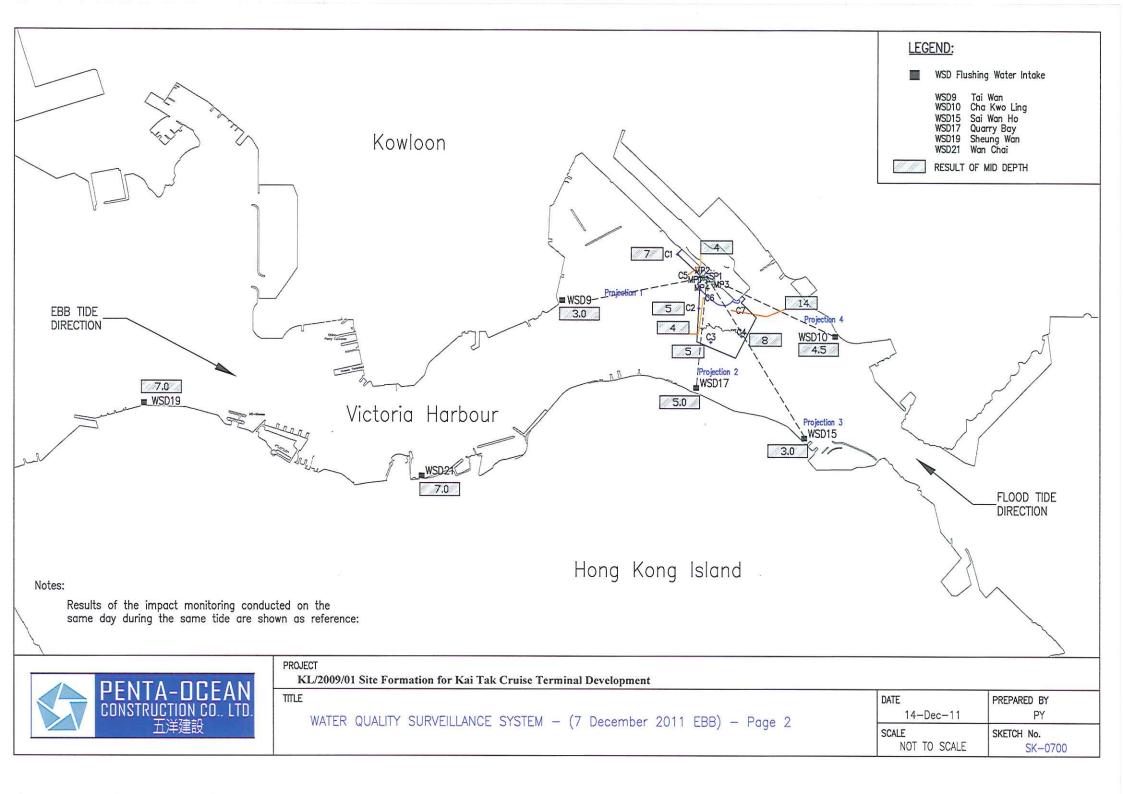


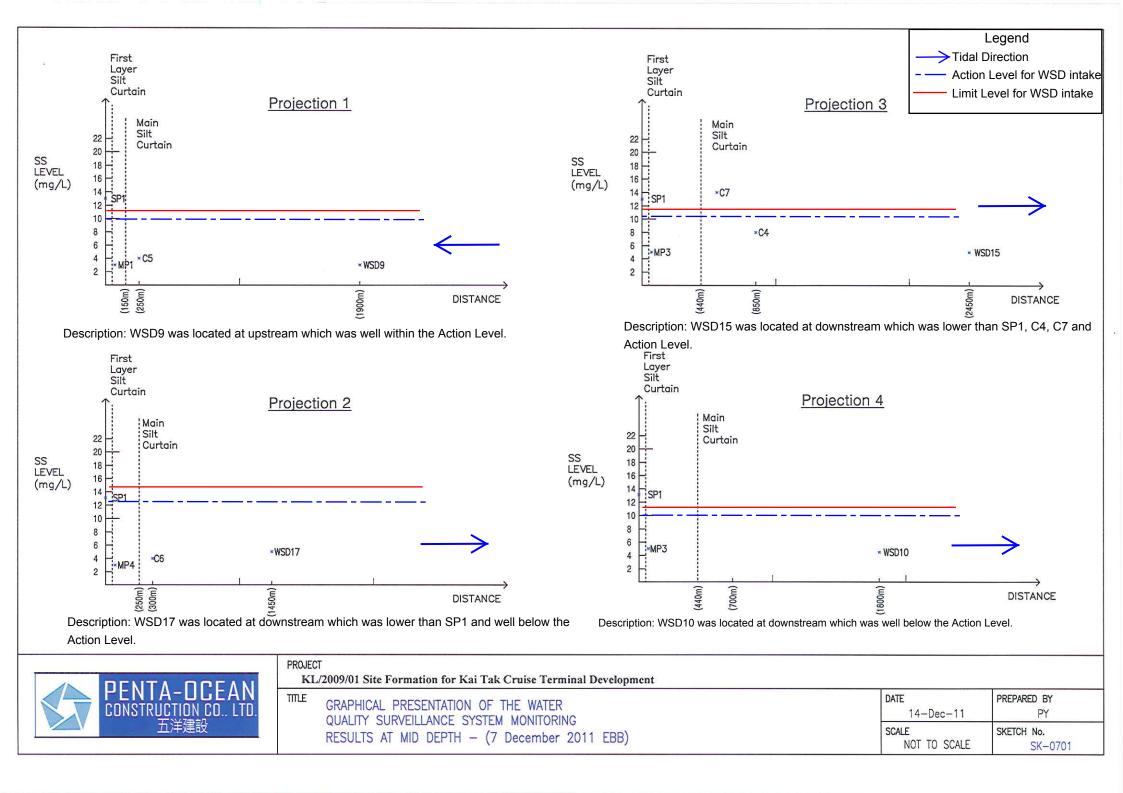



Water Quality Surveillance System Monitoring Results - 23 December 2011 (Flood Tide)

Мо	nitoring Location	Turbidity in NTU	Compare to Trigger Level	Suspended Solids in mg/L	Compare to Trigger Level
	1m below the surface	5.14	N/A	8	00 N/A
SP1	mid depth	4.63	N/A	9	N/A
	1m above the seabed	3.21	N/A	7	N/A
	1m below the surface	2.57	N/A	9	N/A
MP1	mid depth	2.57	N/A	6	N/A
	1m above the seabed	3.40	N/A	11	N/A
	1m below the surface	3.21	N/A	10	N/A
MP2	mid depth	3.23	N/A	9	N/A
	1m above the seabed	2.63	N/A	6	N/A
	1m below the surface	3.18	N/A	9	N/A
MP3	mid depth	3.77	N/A	8	N/A
	1m above the seabed	3.16	N/A	4	N/A
	1m below the surface	2.98	N/A	13	N/A
MP4	mid depth	3.92	N/A	10	N/A
	1m above the seabed	2.52	N/A	8	N/A
	1m below the surface	3.03	Lower	14	Equal
C1	mid depth	3.05	Lower	11	Lower
	1m above the seabed	4.43	Lower	14	Equal
	1m below the surface	3.64	Lower	15	Higher
C2	mid depth	4.60	Lower	13	Lower
	1m above the seabed	4.61	Lower	7	Lower
	1m below the surface	2.71	Lower	10	Lower
C3	mid depth	2.54	Lower	9	Lower
	1m above the seabed	2.90	Lower	8	Lower
	1m below the surface	2.50	Lower	9	Lower
C4	mid depth	2.49	Lower	12	Lower
	1m above the seabed	2.61	Lower	9	Lower
	1m below the surface	3.43	N/A	9	N/A
C5	mid depth	3.17	N/A	5	N/A
	1m above the seabed	2.94	N/A	5	N/A
	1m below the surface	2.01	N/A	7	N/A
C6	mid depth	2.49	N/A	9	N/A
	1m above the seabed	3.13	N/A	10	N/A
	1m below the surface	2.09	N/A	8	N/A
C7	mid depth	1.94	N/A	9	N/A
	1m above the seabed	2.18	N/A	8	N/A

Control	Trigger Level for Turbidity in	Trigger Level for SS in mg/L for Dry Season
Point	NTU for All Season	(October - March)
C1	12.3 for Flood Tide	
C2	12.3 for Flood Tide	14.0
C3	16.9	14.0
C4	10.5 for Ebb Tide	

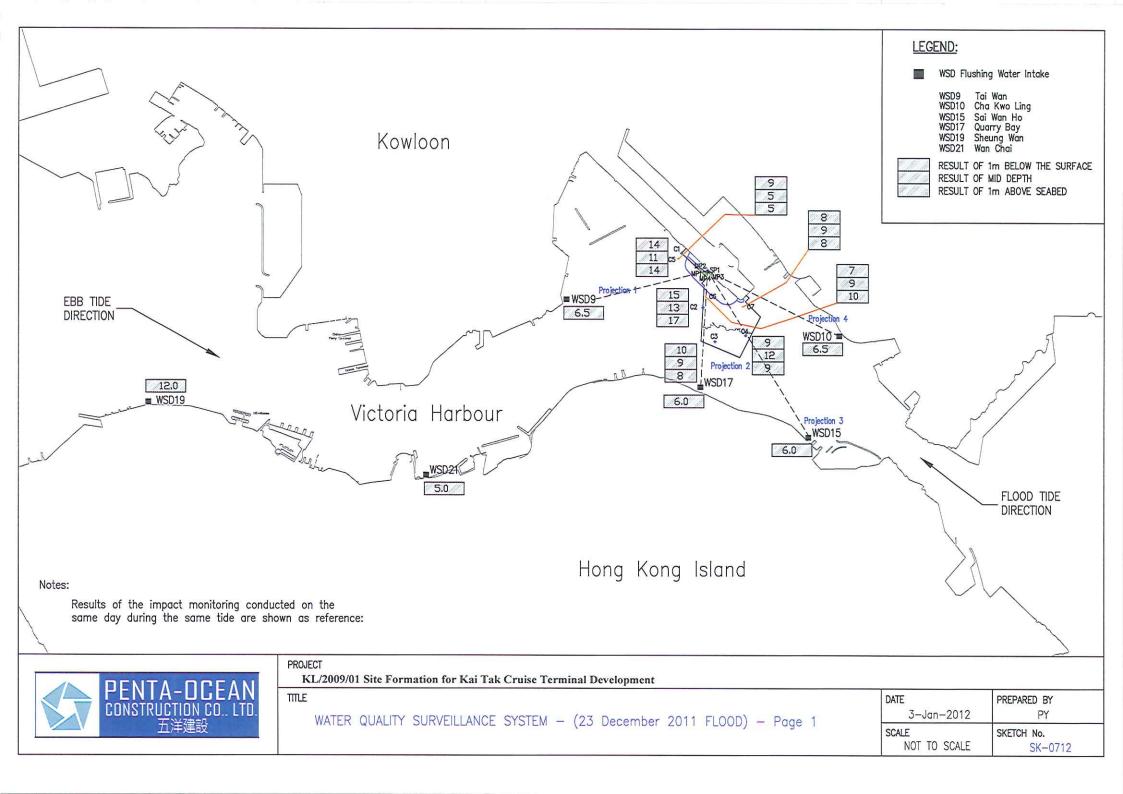

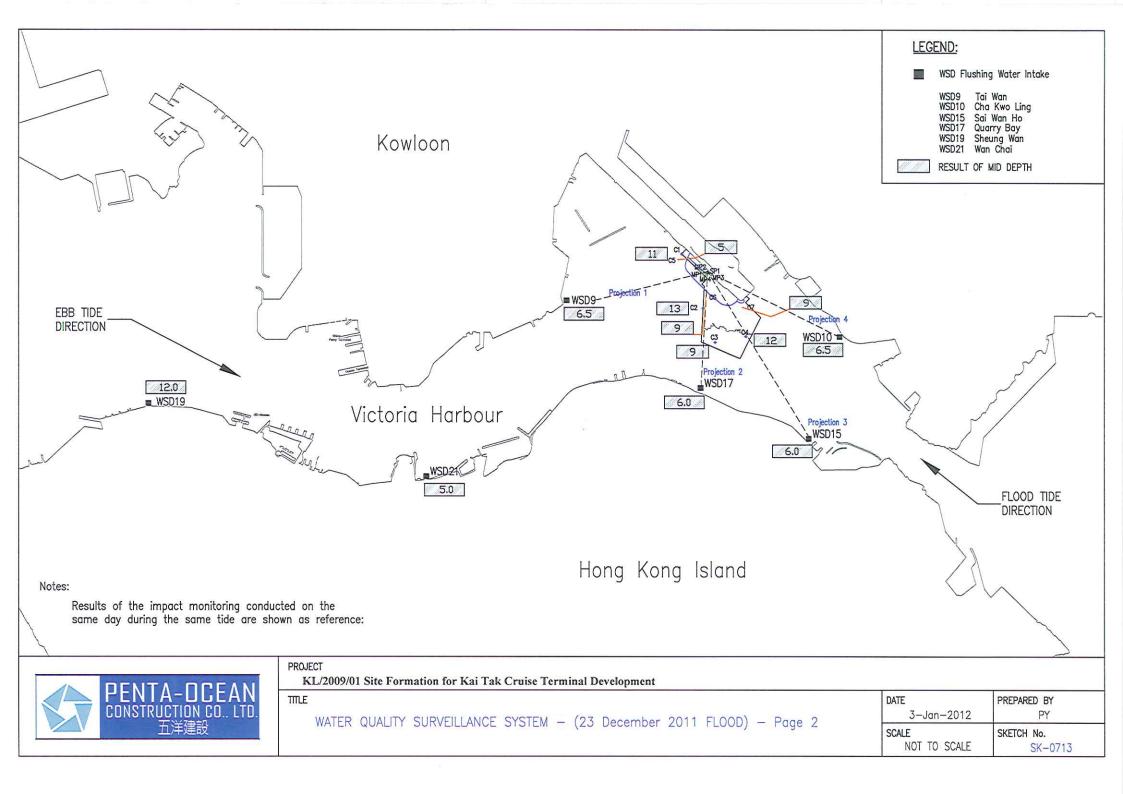

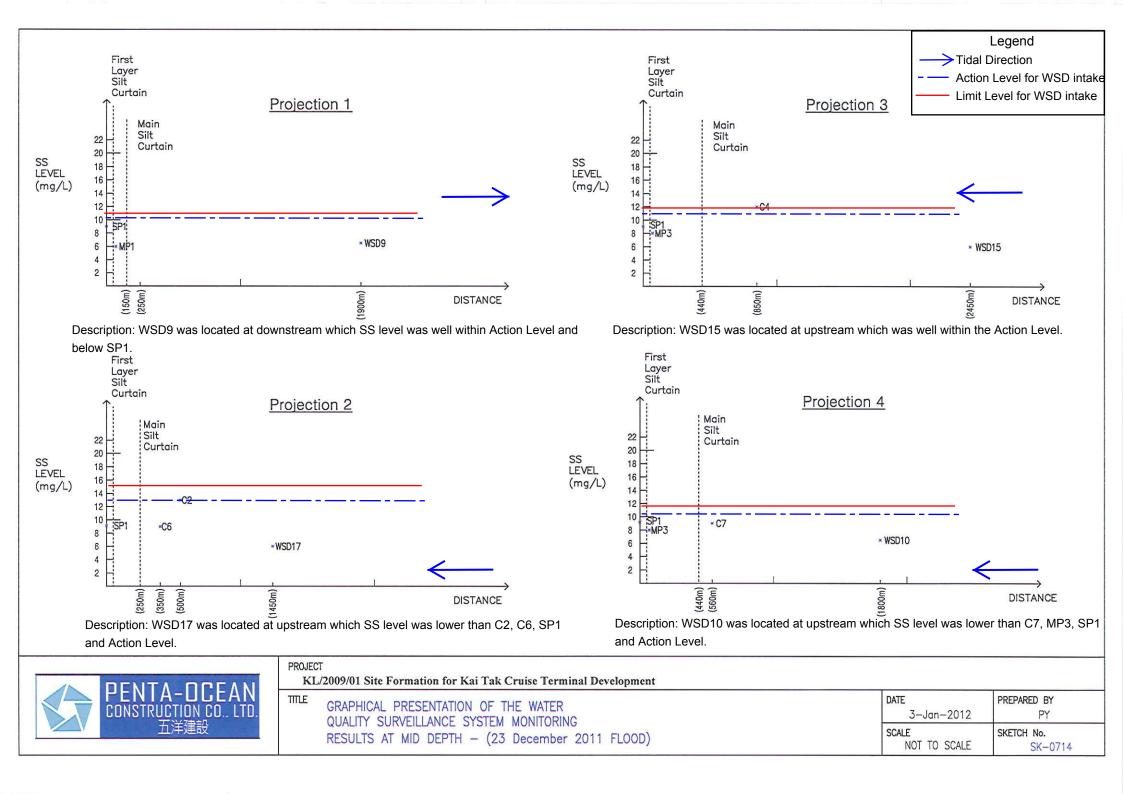



Water Quality Surveillance System Monitoring Results - 12 January 2012 (Flood Tide)


•

Monitoring Location		Turbidity in	Compare to	Suspended	Compare to
5m - 1		NTU	Trigger Level	Solids in mg/L	Trigger Leve
22.1	1m below the surface	6.25	N/A	14	N/A
SP1	mid depth	6.21	N/A	14	N/A
	1m above the seabed	5.54	N/A	16	N/A
	1m below the surface	3.18	N/A	8	N/A
MP1	mid depth	2.77	N/A	7	N/A
	1m above the seabed	3.39	N/A	7	N/A
	1m below the surface	2.33	N/A	8	N/A
MP2	mid depth	2.67	N/A	6	N/A
Description of the	1m above the seabed	2.63	N/A	8	N/A
	1m below the surface	2.11	N/A	3	N/A
MP3	mid depth	2.10	N/A	7	N/A
	1m above the seabed	1.99	N/A	6	N/A
	1m below the surface	2.10	N/A	5	N/A
MP4	mid depth	1.88	N/A	9	N/A
	1m above the seabed	2.51	N/A	6	N/A
	1m below the surface	2.01	Lower	8	Lower
C1	mid depth	2.42	Lower	4	Lower
	1m above the seabed	2.35	Lower	6	Lower
	1m below the surface	1.85	Lower	4	Lower
C2	mid depth	2.05	Lower	4	Lower
	1m above the seabed	1.24	Lower	6	Lower
	1m below the surface	2.10	Lower	5	Lower
C3	mid depth	2.61	Lower	7	Lower
	1m above the seabed	2.33	Lower	10	Lower
	1m below the surface	2.08	Lower	4	Lower
C4	mid depth	1.99	Lower	8	Lower
	1m above the seabed	2.10	Lower	6	Lower
	1m below the surface	2.75	N/A	7	N/A
C5	mid depth	1.55	N/A	6	N/A
	1m above the seabed	2.34	N/A	7	N/A
200	1m below the surface	2.02	N/A	7	N/A
C6	mid depth	1.86	N/A	5	N/A
	1m above the seabed	1.98	N/A	4	N/A
	1m below the surface	2.89	N/A	7	N/A
C7	mid depth	1.90	N/A	7	N/A
07	1m above the seabed	2.39	N/A	5	N/A N/A

Control Point	Trigger Level for Turbidity in NTU for All Season	Trigger Level for SS in mg/L for Dry Season (October - March)
C1	12.3 for Flood Tide	14.0
C2	12.3 for Flood Tide	
C1 C2 C3	16.9	
C4	10.5 for Ebb Tide	

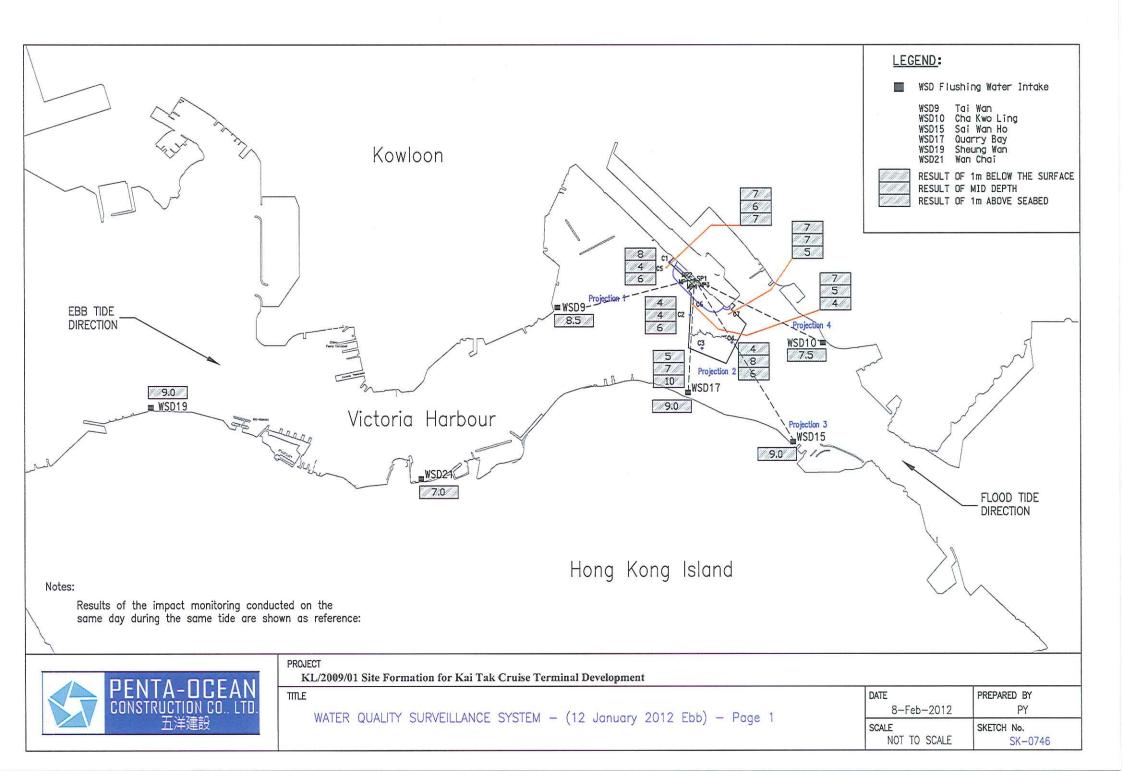

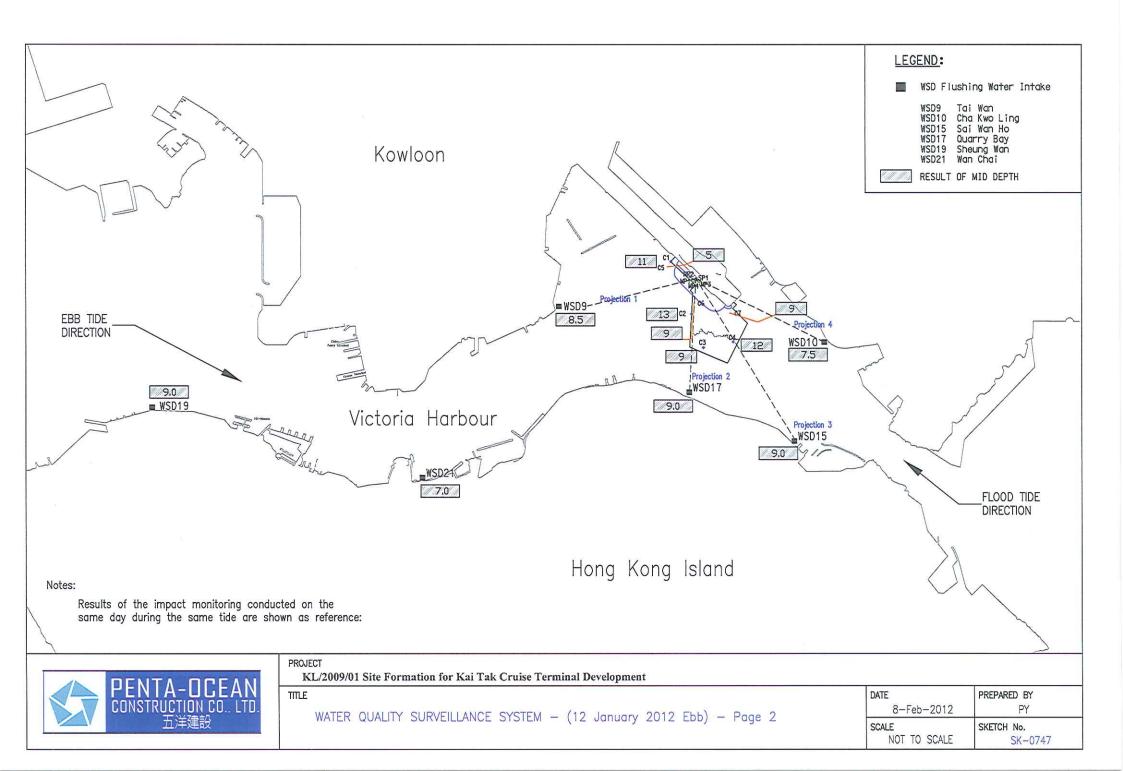


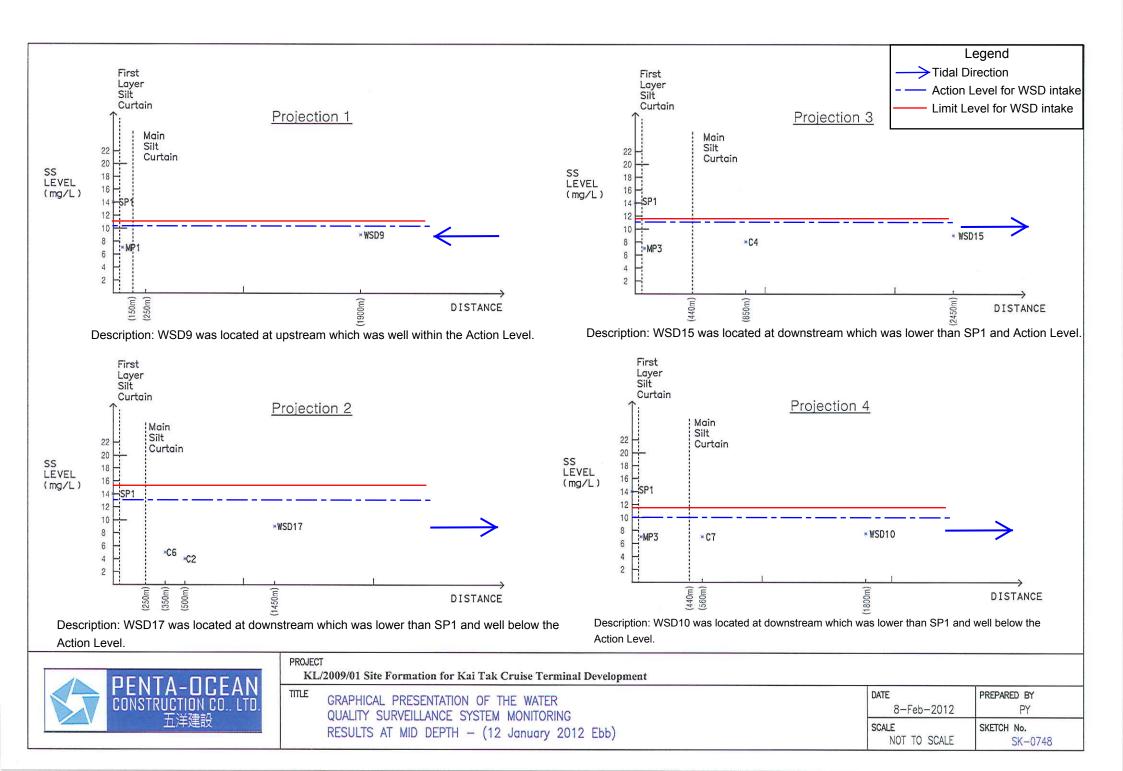



Water Quality Surveillance System Monitoring Results - 20 January 2012 (Flood Ti	de)
Water Quality but ventance bystem Monitoring Results - 20 January 2012 (1900) 11	uc

Mo	nitoring Location	Turbidity in	Compare to	Suspended	Compare to
IVIO		NTU	Trigger Level	Solids in mg/L	Trigger Level
	1m below the surface	5.00	N/A	9	N/A
SP1	mid depth	5.15	N/A	9	N/A
	1m above the seabed	5.59	N/A	8	N/A
	1m below the surface	5.13	N/A	10	N/A
MP1	mid depth	4.70	N/A	7	N/A
	1m above the seabed	3.12	N/A	13	N/A
	1m below the surface	2.44	N/A	4	N/A
MP2	mid depth	2.65	N/A	6	N/A
	1m above the seabed	2.92	N/A	4	N/A
	1m below the surface	2.46	N/A	6	N/A
MP3	mid depth	2.71	N/A	3	N/A
	1m above the seabed	1.95	N/A	3	N/A
	1m below the surface	2.71	N/A	7	N/A
MP4	mid depth	3.55	N/A	6	N/A
	1m above the seabed	2.59	N/A	6	N/A
	1m below the surface	2.16	Lower	6	Lower
C1	mid depth	2.44	Lower	6	Lower
	1m above the seabed	2.54	Lower	6	Lower
	1m below the surface	2.83	Lower	4	Lower
C2	mid depth	1.95	Lower	3	Lower
	1m above the seabed	1.50	Lower	3	Lower
	1m below the surface	2.24	Lower	3	Lower
C3	mid depth	1.83	Lower	4	Lower
	1m above the seabed	1.71	Lower	<2	Lower
	1m below the surface	1.84	Lower	6	Lower
C4	mid depth	1.56	Lower	<2	Lower
	1m above the seabed	1.74	Lower	6	Lower
	1m below the surface	2.11	N/A	6	N/A
C5	mid depth	2.23	N/A	7	N/A
	1m above the seabed	2.30	N/A	4	N/A
	1m below the surface	2.82	N/A	5	N/A
C6	mid depth	1.77	N/A	- 5	N/A
	1m above the seabed	2.00	N/A	3	N/A
	1m below the surface	2.05	N/A	4	N/A
C7	mid depth	1.68	N/A	3	N/A
	1m above the seabed	2.00	N/A	7	N/A

Control	Trigger Level for Turbidity in	Trigger Level for SS in mg/L for Dry Season
Point	NTU for All Season	(October - March)
C1	12.3 for Flood Tide	
C2	12.3 for Flood Tide	14.0
C3	16.9	14.0
C4	10.5 for Ebb Tide	

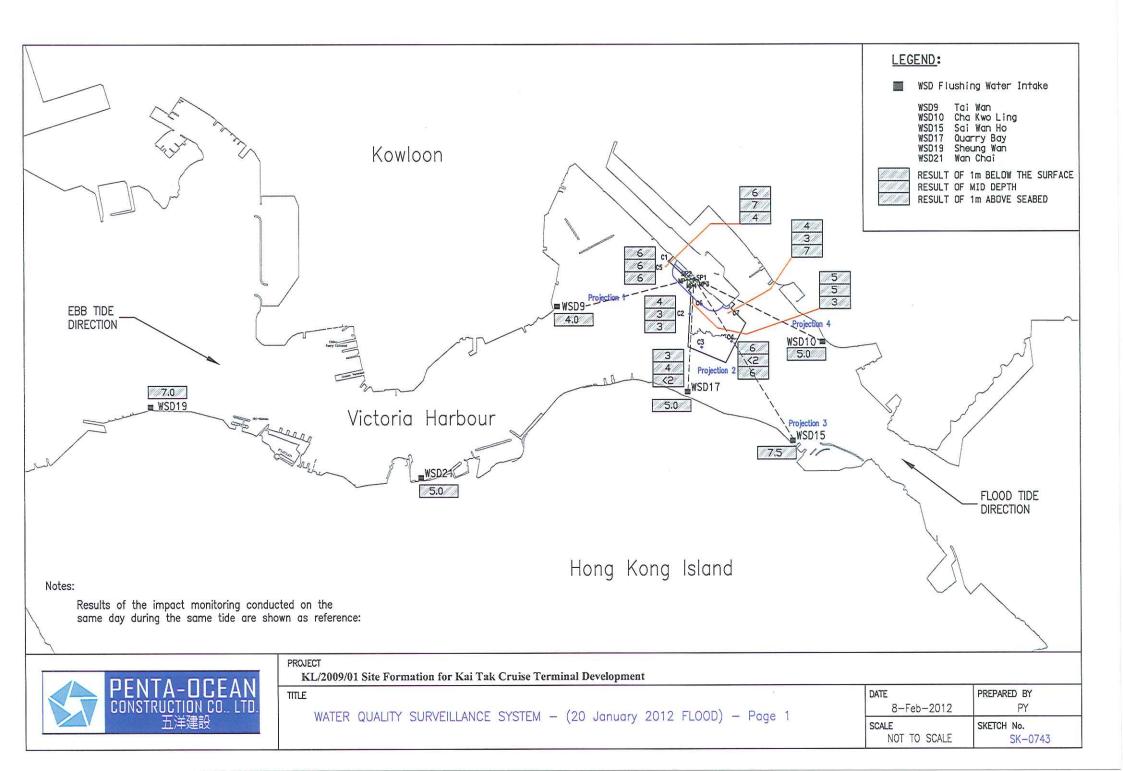

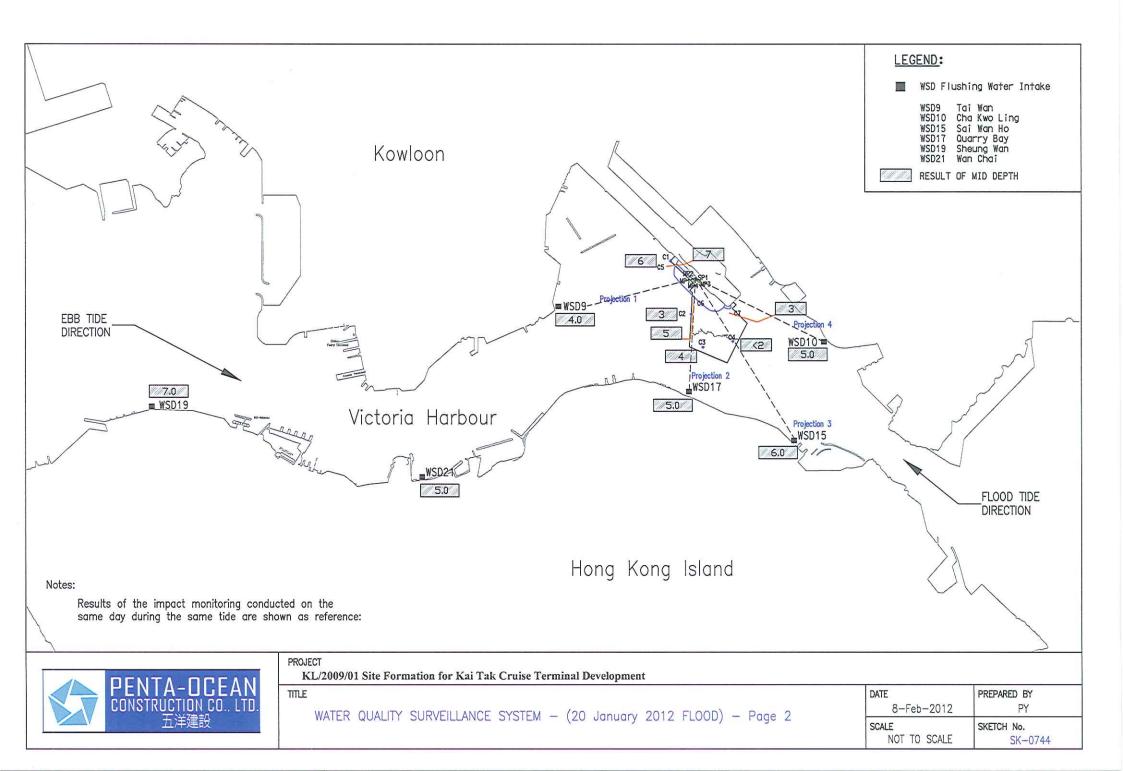


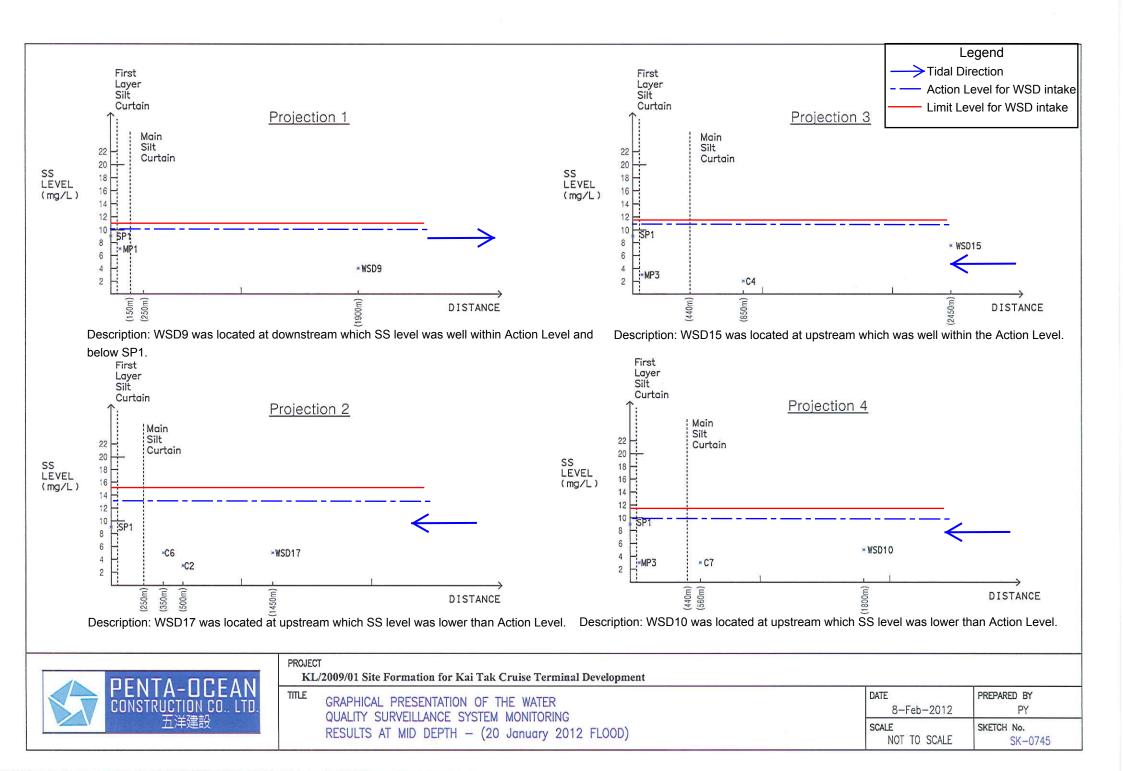



Мо	nitoring Location	Turbidity in	Compare to	Suspended	Compare to
		NTU	Trigger Level	Solids in mg/L	Trigger Leve
SP1	1m below the surface	27.0	N/A	56	N/A
	mid depth	13.6	N/A	32	N/A
141	1m above the seabed	8.54	N/A	16	N/A
	1m below the surface	2.76	N/A	11	N/A
MP1	mid depth	1.44	N/A	11	N/A
	1m above the seabed	2.08	N/A	8	N/A
	1m below the surface	2.53	N/A	9	N/A
MP2	mid depth	2.32	N/A	8	N/A
	1m above the seabed	1.90	N/A	13	N/A
	1m below the surface	2.17	N/A	10	N/A
MP3	mid depth	2.23	N/A	5	N/A
	1m above the seabed	2.21	N/A	5	N/A
	1m below the surface	1.80	N/A	10	N/A
MP4	mid depth	2.21	N/A	8	N/A
	1m above the seabed	2.17	N/A	9	N/A
	1m below the surface	1.82	Lower	5	Lower
C1	mid depth	2.26	Lower	8	Lower
	1m above the seabed	1.68	Lower	8	Lower
	1m below the surface	1.91	Lower	8	Lower
C2	mid depth	2.01	Lower	5	Lower
	1m above the seabed	1.65	Lower	6	Lower
	1m below the surface	2.82	Lower	7	Lower
C3	mid depth	2.41	Lower	8	Lower
	1m above the seabed	2.59	Lower	10	Lower
	1m below the surface	2.07	Lower	19	Higher
C4	mid depth	1.72	Lower	10	Lower
	1m above the seabed	2.33	Lower	21	Higher
	1m below the surface	2.03	N/A	4	N/A
C5	mid depth	1.95	N/A	7	N/A
	1m above the seabed	2.14	N/A	4	N/A
	1m below the surface	1.61	N/A	8	N/A
C6	mid depth	2.28	N/A	8	N/A
00	1m above the seabed	2.44	N/A	6	N/A
	1m below the surface	2.14	N/A	8	N/A
C7	mid depth	1.97	N/A N/A	6	N/A
C/	1m above the seabed	1.97	N/A N/A	8	N/A

Water Quality Surveillance System Monitoring Results - 10 February 2012 (Ebb Tide)

Control	Trigger Level for Turbidity in	Trigger Level for SS in mg/L for Dry Season
Point	NTU for All Season	(October - March)
C1	12.3 for Flood Tide	
C2	12.3 for Flood Tide	14.0
C3	16.9	14.0
C4	10.5 for Ebb Tide	

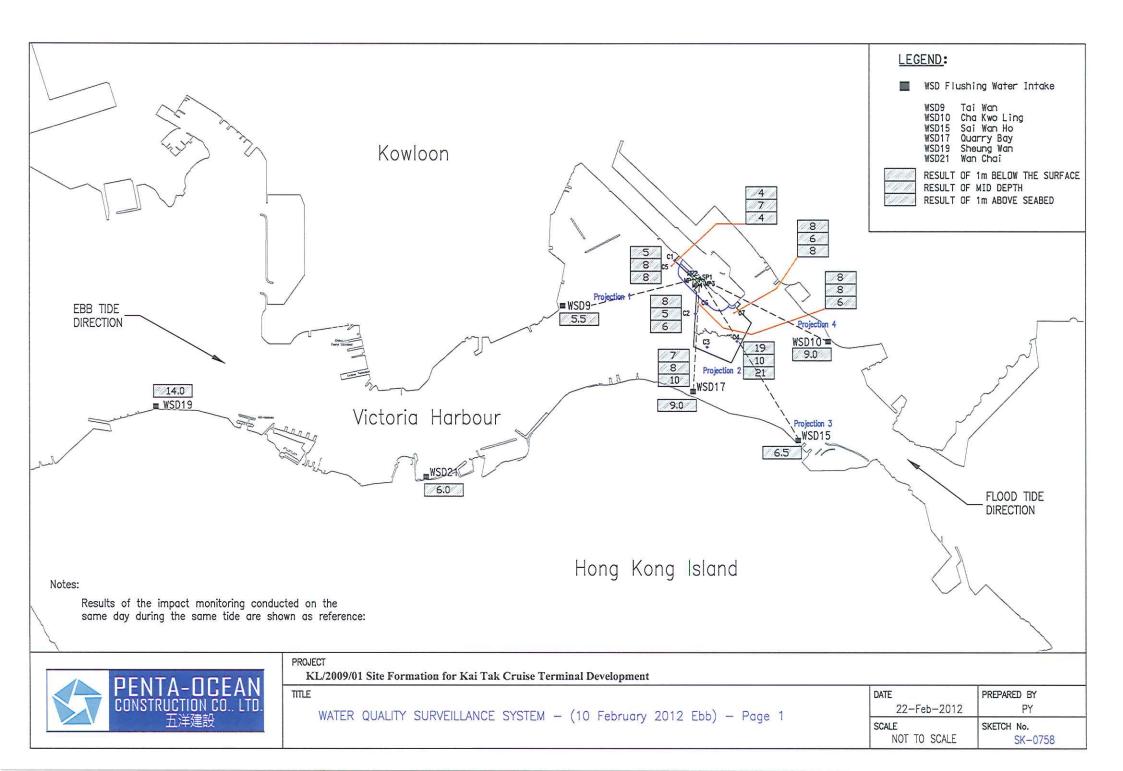

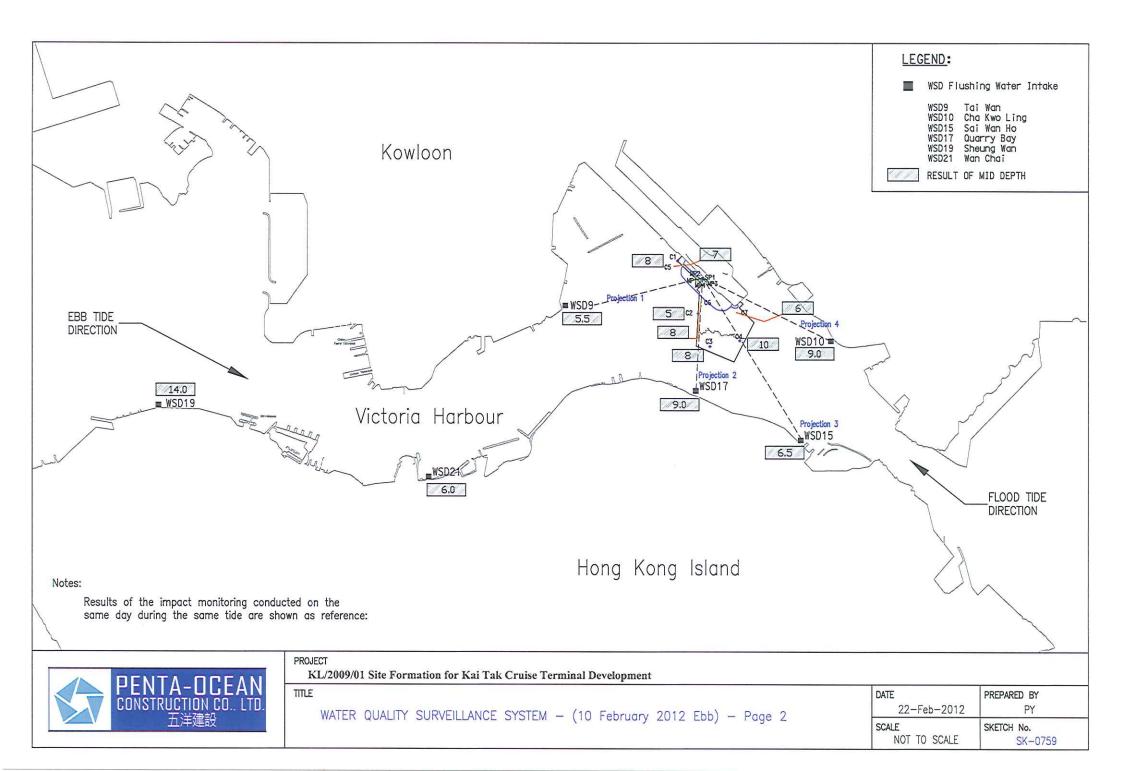


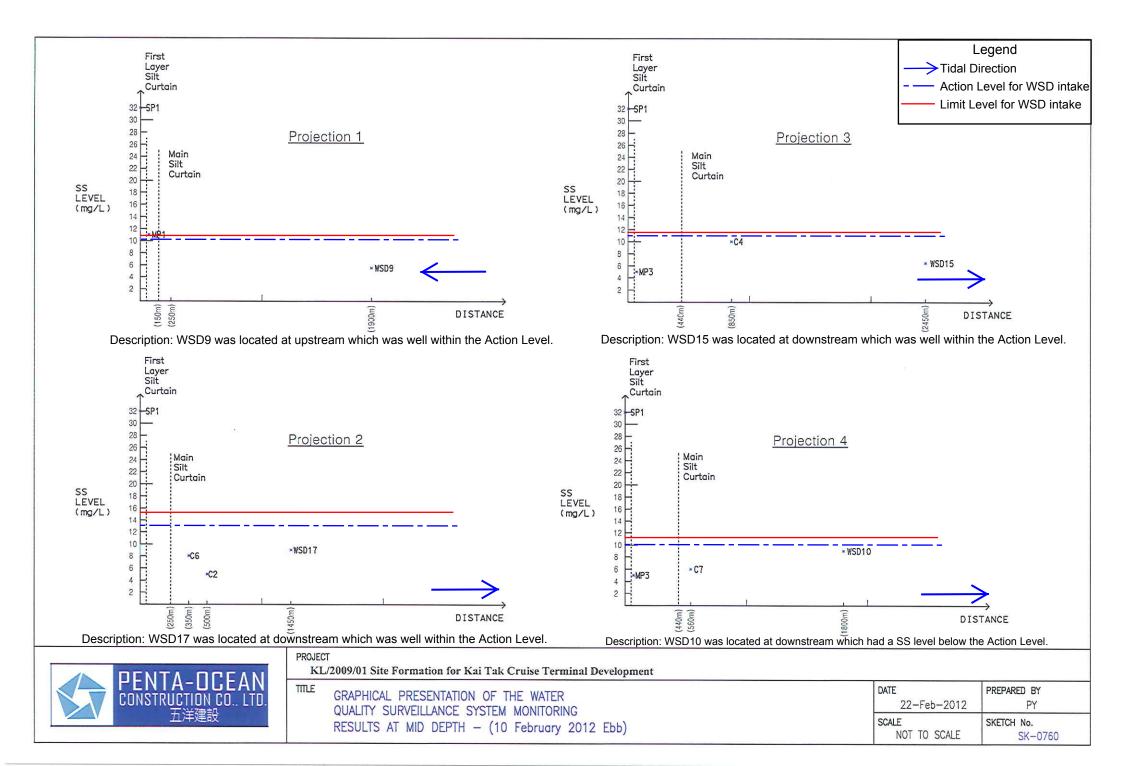



Мо	nitoring Location	Turbidity in NTU	Compare to Trigger Level	Suspended Solids in mg/L	Compare to Trigger Level
	1m below the surface	6.19	N/A	13	N/A
SP1	mid depth	4.98	N/A	8	N/A
	1m above the seabed	5.78	N/A	10	N/A
	1m below the surface	1.97	N/A	7	N/A
MP1	mid depth	1.76	N/A	4	N/A
	1m above the seabed	2.18	N/A	5	N/A
	1m below the surface	2.13	N/A	4	N/A
MP2	mid depth	2.24	N/A	4	N/A
	1m above the seabed	1.70	N/A	8	N/A
	1m below the surface	2.27	N/A	2	N/A
MP3	mid depth	1.61	N/A	4	N/A
	1m above the seabed	2.02	N/A	3	N/A
	1m below the surface	2.04	N/A	4	N/A
MP4	mid depth	1.86	N/A	4	N/A
	1m above the seabed	1.31	N/A	4	N/A
	1m below the surface	1.86	Lower	9	Lower
C1	mid depth	1.86	Lower	5	Lower
	1m above the seabed	2.17	Lower	6	Lower
	1m below the surface	2.42	Lower	6	Lower
C2	mid depth	1.75	Lower	4	Lower
	1m above the seabed	1.63	Lower	4	Lower
	1m below the surface	2.20	Lower	6	Lower
C3	mid depth	2.21	Lower	6	Lower
	1m above the seabed	2.32	Lower	4	Lower
	1m below the surface	1.70	Lower	4	Lower
C4	mid depth	2.16	Lower	3	Lower
	1m above the seabed	2.07	Lower	4	Lower
	1m below the surface	2.85	N/A	4	N/A
C5	mid depth	2.06	N/A	5	N/A
	1m above the seabed	2.63	N/A	11	N/A
	1m below the surface	1.71	N/A	3	N/A
C6	mid depth	1.58	N/A	3	N/A
	1m above the seabed	1.36	N/A	4	N/A
	1m below the surface	2.09	N/A	6	N/A
C7	mid depth	2.11	N/A	6	N/A
	1m above the seabed	1.84	N/A	10	N/A

Water Quality Surveillance System Monitoring Results - 20 February 2012 (Flood Tide)

Control	Trigger Level for Turbidity in	Trigger Level for SS in mg/L for Dry Season
Point	NTU for All Season	(October - March)
C1	12.3 for Flood Tide	
C2	12.3 for Flood Tide	14.0
C3	16.9	14.0
C4	10.5 for Ebb Tide	

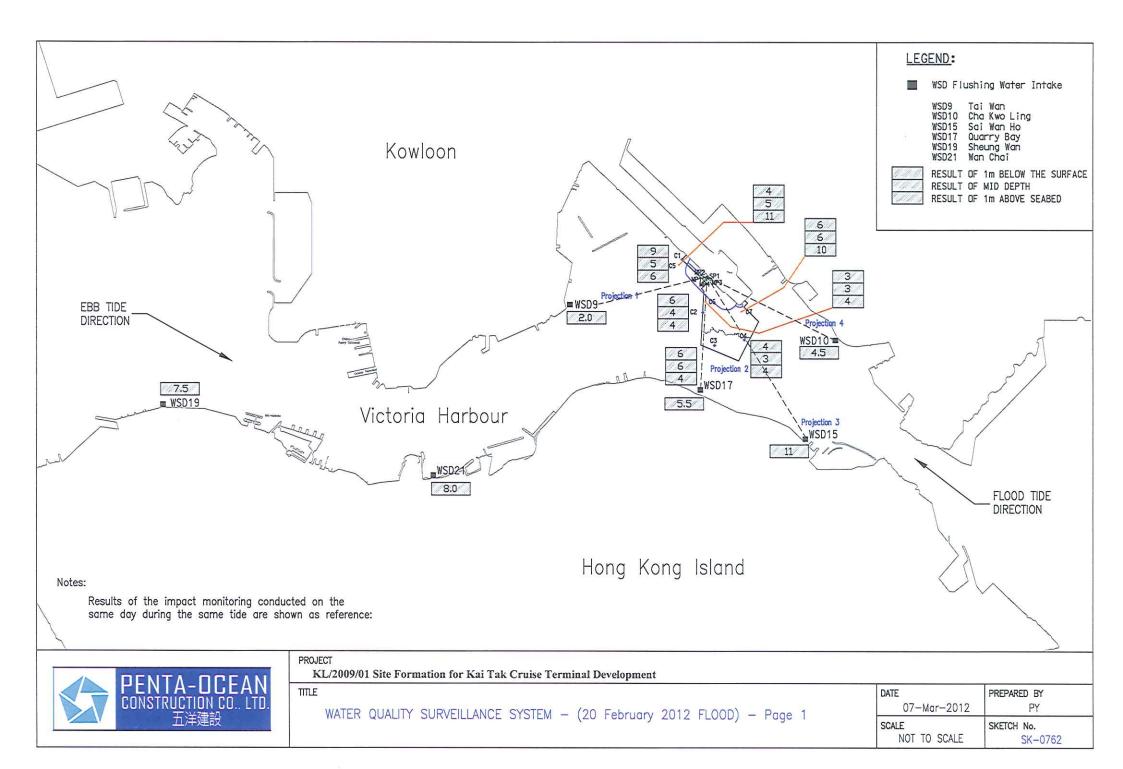

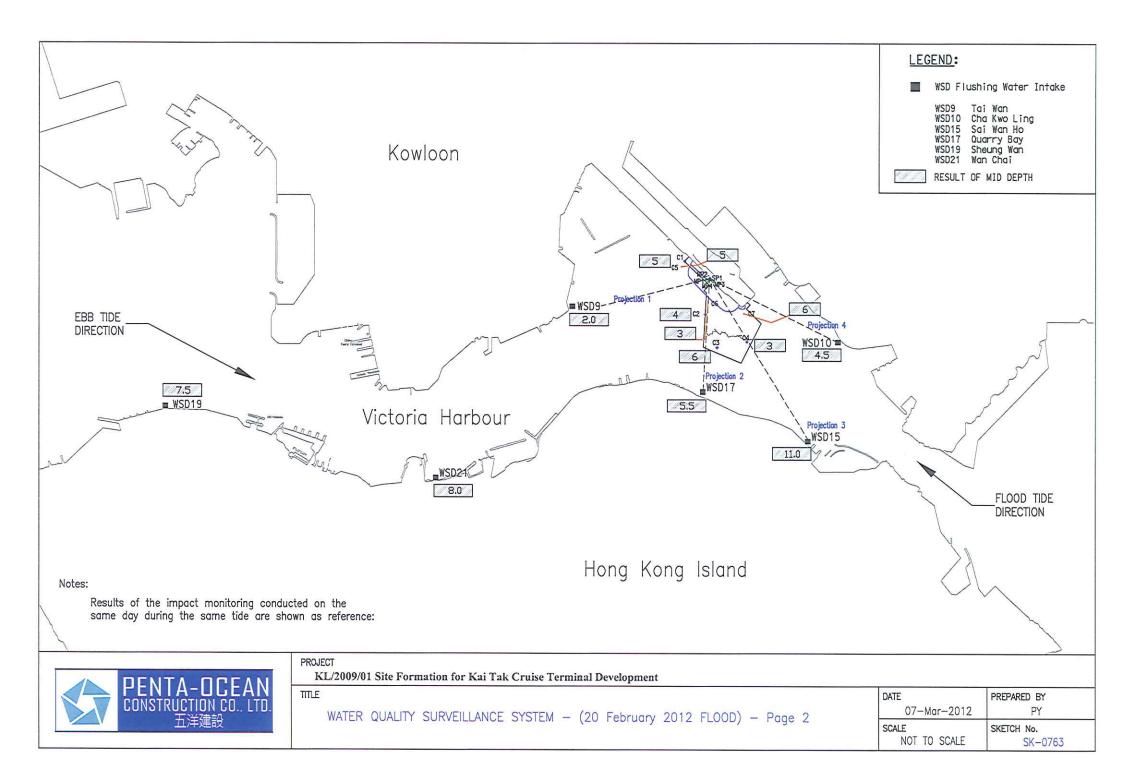

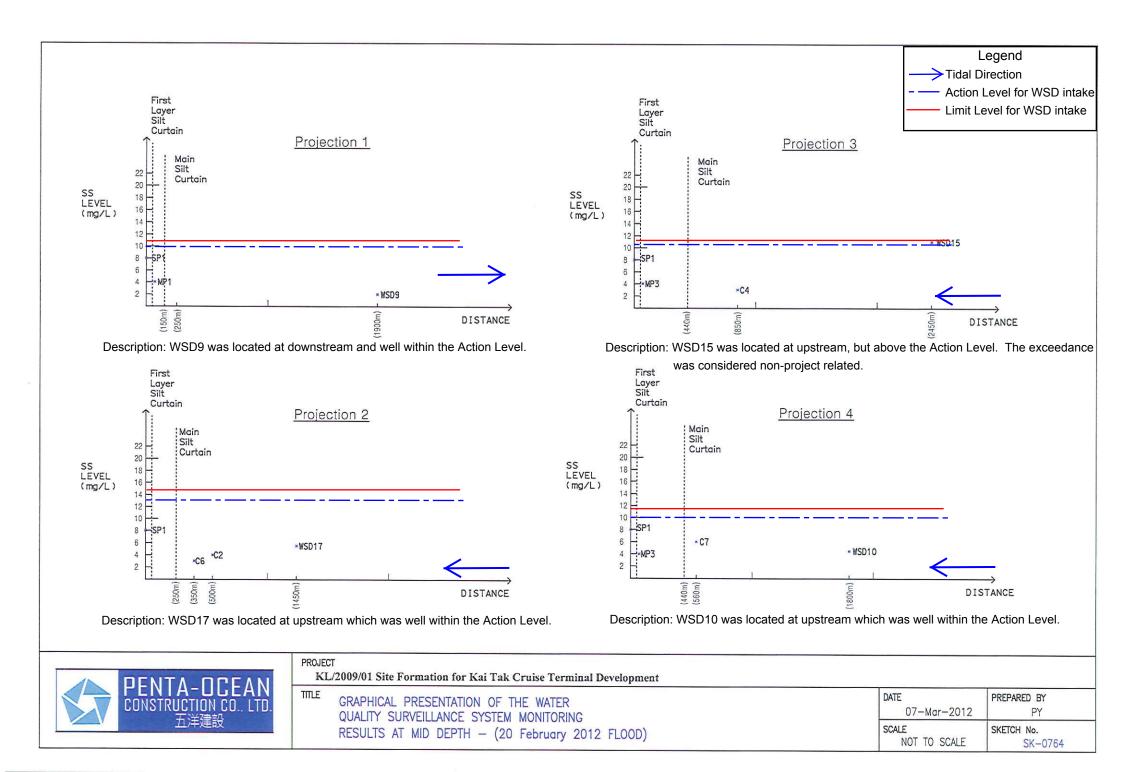



Appendix 5.1

Event and Action Plan



Event and Action Plan for Construction Noise

EVENT	ACTION			
	ET	IC(E)	ER	CONTRACTOR
Action Level	 Notify IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, ER and Contractor; Discuss with the Contractor and formulate remedial measures; Increase monitoring frequency to check mitigation effectiveness. 	 Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented. 	 Submit noise mitigation proposals to IEC; Implement noise mitigation proposals.
Limit Level	 Identify source; Inform IEC, ER, EPD and Contractor; Repeat measurements to confirm findings; Increase monitoring frequency; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Inform IEC, ER and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. 	 Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Submit further proposal if problem still not under control; Stop the relevant portion of works as instructed by the ER until the exceedance is abated.



Event and Action Plan for Marine Water Quality

EVENT	ACTION					
	ET	IEC	ER	CONTRACTOR		
Action level being exceeded by one sampling day	 Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next day of exceedance. 	 Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified) 	 Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. (The above actions should be taken within 1 working day after the exceedance is identified) 	 Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Review the working methods and consider additional measures such as use of frame- type silt curtain, deployment of double silt curtains, slowing down, or rescheduling of works; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified) 		
Action level being exceeded by more than one consecutive sampling days	 Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; 	 Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER 	 Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness 	 Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and 		



EVENT	ACTION						
	ET	IEC	ER	CONTRACTOR			
	 Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next working day of exceedance. 	accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 4. (The above actions should be taken within 1 working day after the exceedance is identified)	of the implemented mitigation measures. 4. (The above actions should be taken within 1 working day after the exceedance is identified)	 equipment; 4. Review the working methods and consider additional measures such as use of frame- type silt curtain, deployment of double silt curtains, slowing down, or rescheduling of works; 5. Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation measures. 7. (The above actions should be taken within 1 working day after the exceedance is identified) 			



EVENT	ACTION					
	ET	IEC	ER	CONTRACTOR		
Limit level being exceeded by one sampling day	 Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC, Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit Level. (The above actions should be taken within 1 working day after the exceedance is identified) 	 Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified) 	 Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified) 	 Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Review the working methods and consider additional measures such as use of frame- type silt curtain, deployment of double silt curtains, slowing down, or rescheduling of works; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified) 		



EVENT	ACTION					
	ET	IEC	ER	CONTRACTOR		
Limit level being exceeded by more than one consecutive sampling days	 Identify source(s) of impact; Inform IEC, Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. (The above actions should be taken within 1 working day after the exceedance is identified) 	 Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified) 	 Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified) 	 Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Review the working methods and consider additional measures such as use of frame- type silt curtain, deployment of double silt curtains, slowing down, or rescheduling of works; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures; As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities. (The above actions should be taken within 1 working day after the exceedance is identified) 		



Appendix 5.2


Graphic Presentation of SS Results against to Tidal Movement along Victoria Harbour

Contract no. KL/2009/01 Site Formation for Kai Tak Cruise Terminal Development Summary of Recorded Exceedances in Reporting Quarter

Date	Tide	Station	Parameter	Evcoodanco	Turbidity (NTU) / SS (mg/L) value	Possible Cause of Exceedance	Turbidity (NTU) / SS (mg/L) value in the nearest upstream station
20/2/2012	Mid-flood	WSD15	SS (mg/L)	AL	11	Upstream of the Project	N/A



Graphic Presentation of SS Results Against the Tidal Movement along Victoria Harbour

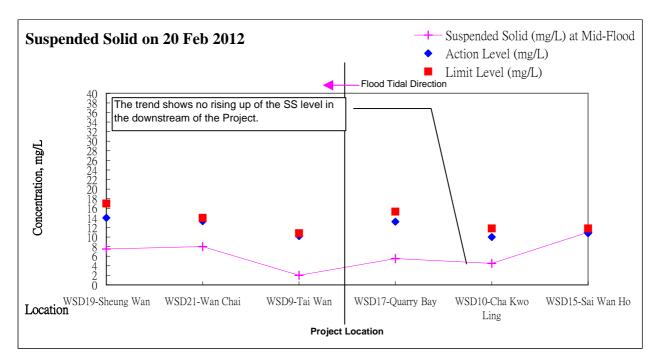




Appendix 5.3

Graphic Presentation of Water Quality Result with respect to Local Variation


am

Graphic Presentation of Water Quality Result of WSD9 - Tai Wan with respect to Local Variation

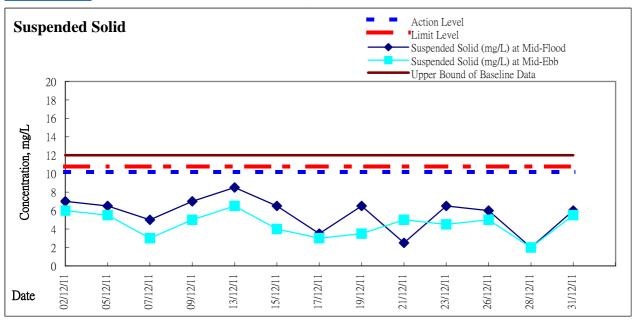


Remarks: WSD9 is located at upstream during the ebb tides while at downstream during flood tides.

Graphic Presentation of Water Quality Result of WSD10 - Cha Kwo Ling with respect to Local Variation

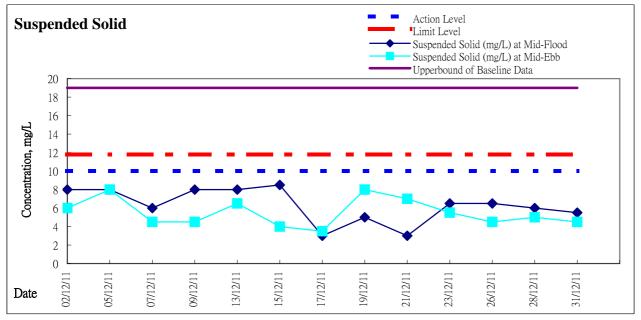


Remarks: WSD10 is located at upstream during the flood tides while at downstream during ebb tides.

Graphic Presentation of Water Quality Result of WSD15 - Sai Wan Ho with respect to Local Variation

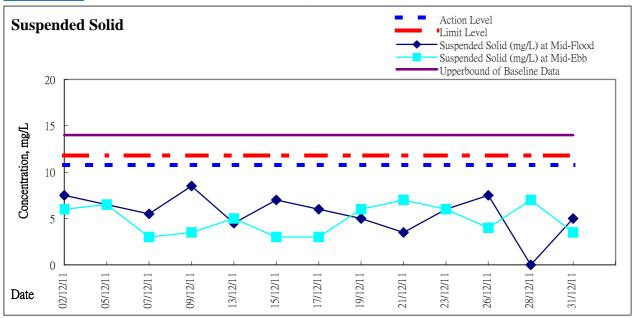


Remarks: WSD15 is located at upstream during the flood tides while at downstream during ebb tides.

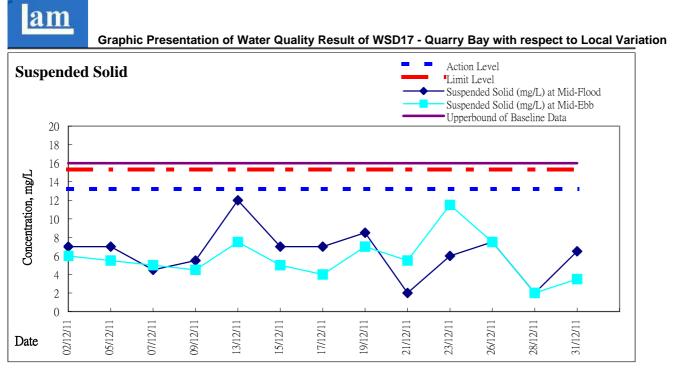


Remarks: WSD17 is located at upstream during the flood tides while at downstream during ebb tides.

Graphic Presentation of Water Quality Result of WSD19 - Sheung Wan with respect to Local Variation

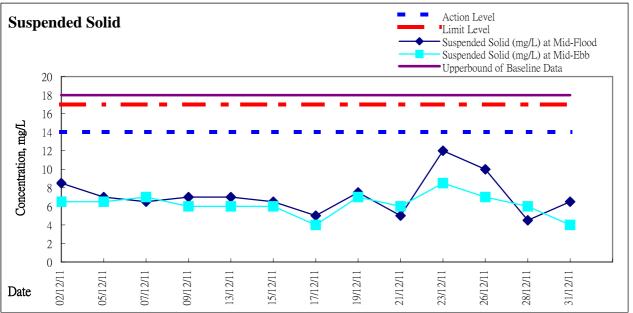


Remarks: WSD19 is located at upstream during the ebb tides while at downstream during flood tides.

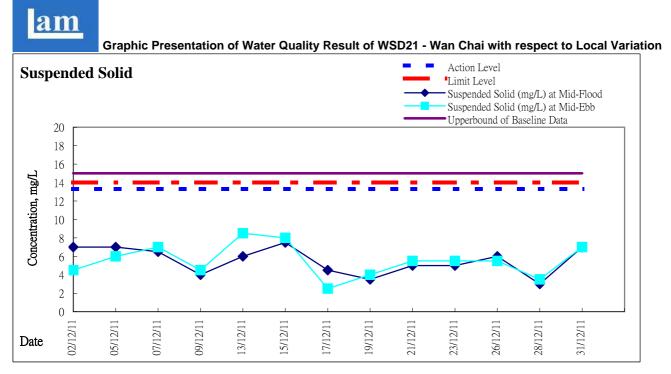

Remarks: WSD21 is located at upstream during the ebb tides while at downstream during flood tides.


am

Graphic Presentation of Water Quality Result of WSD9 - Tai Wan with respect to Local Variation

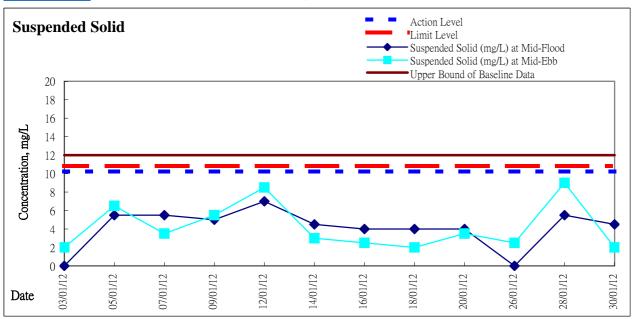

Remarks: WSD9 is located at upstream during the ebb tides while at downstream during flood tides.


Graphic Presentation of Water Quality Result of WSD10 - Cha Kwo Ling with respect to Local Variation

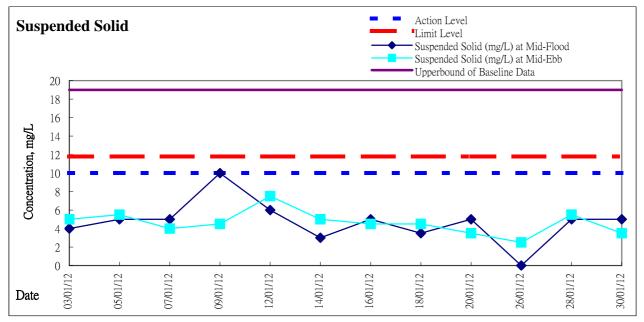


Remarks: WSD10 is located at upstream during the flood tides while at downstream during ebb tides.

Note: With respect to the EPD's no comment on the new Action and Limit Levels for water monitoring on 19 October 2011, the new set Action and Limit Levels for turbidity and SS was applied to used from 19 Oct 2011.

Graphic Presentation of Water Quality Result of WSD15 - Sai Wan Ho with respect to Local Variation

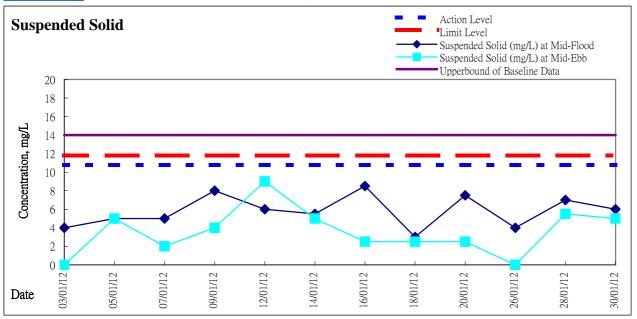


Remarks: WSD15 is located at upstream during the flood tides while at downstream during ebb tides.

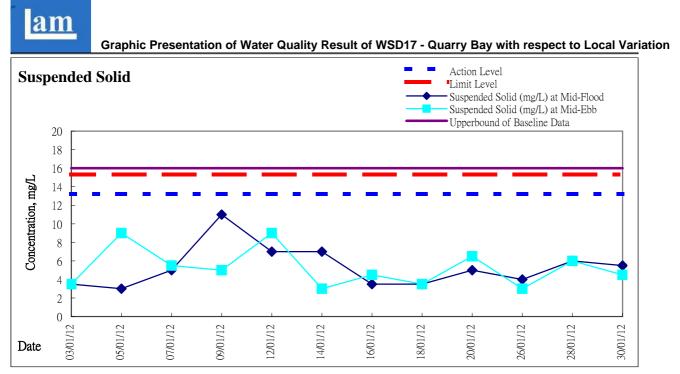


Remarks: WSD17 is located at upstream during the flood tides while at downstream during ebb tides.

Note: With respect to the EPD's no comment on the new Action and Limit Levels for water monitoring on 19 October 2011, the new set Action and Limit Levels for turbidity and SS was applied to used from 19 Oct 2011.

Graphic Presentation of Water Quality Result of WSD19 - Sheung Wan with respect to Local Variation

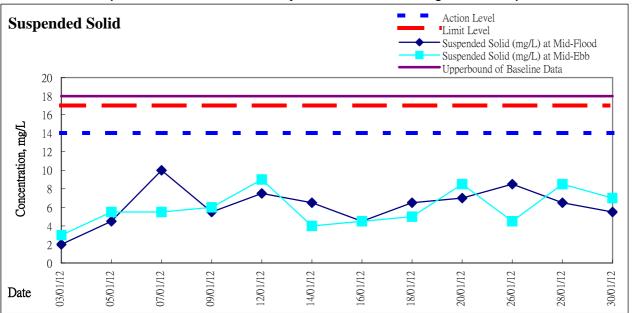

Remarks: WSD19 is located at upstream during the ebb tides while at downstream during flood tides.

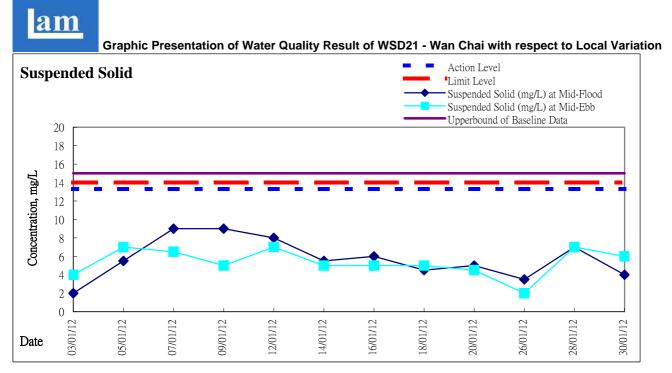


Remarks: WSD21 is located at upstream during the ebb tides while at downstream during flood tides.

Note: With respect to the EPD's no comment on the new Action and Limit Levels for water monitoring on 19 October 2011, the new set Action and Limit Levels for turbidity and SS was applied to used from 19 Oct 2011.


am

Graphic Presentation of Water Quality Result of WSD9 - Tai Wan with respect to Local Variation

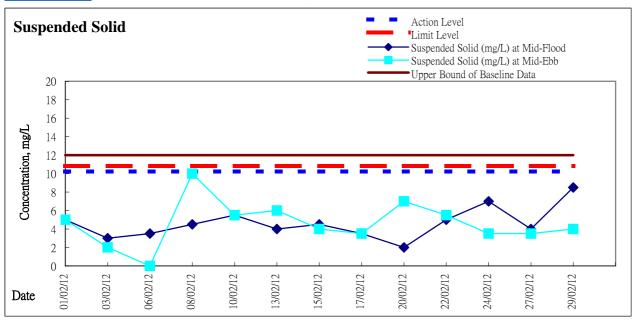


Remarks: WSD9 is located at upstream during the ebb tides while at downstream during flood tides.

Graphic Presentation of Water Quality Result of WSD10 - Cha Kwo Ling with respect to Local Variation

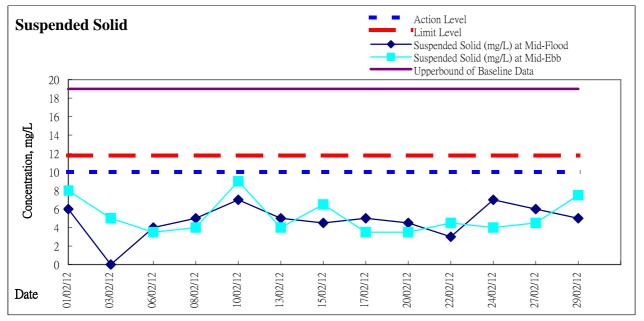


Remarks: WSD10 is located at upstream during the flood tides while at downstream during ebb tides.

Graphic Presentation of Water Quality Result of WSD15 - Sai Wan Ho with respect to Local Variation

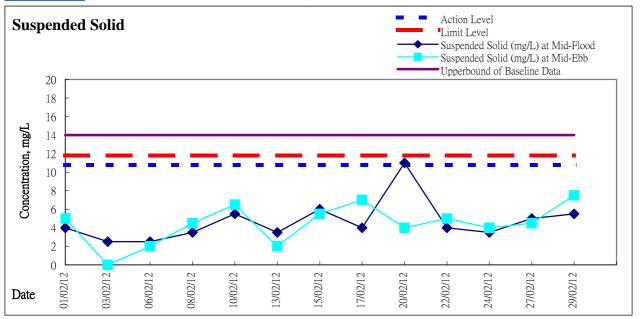


Remarks: WSD15 is located at upstream during the flood tides while at downstream during ebb tides.

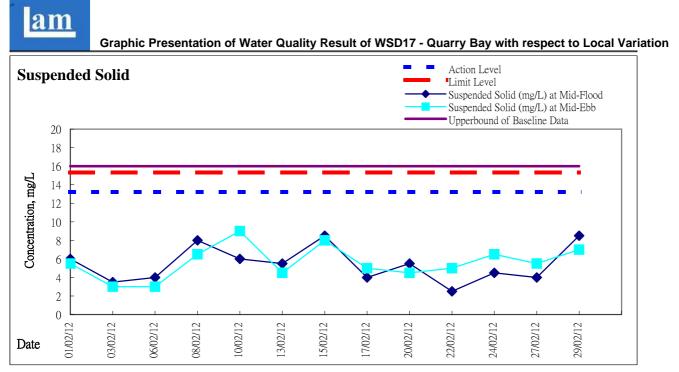


Remarks: WSD17 is located at upstream during the flood tides while at downstream during ebb tides.

Graphic Presentation of Water Quality Result of WSD19 - Sheung Wan with respect to Local Variation

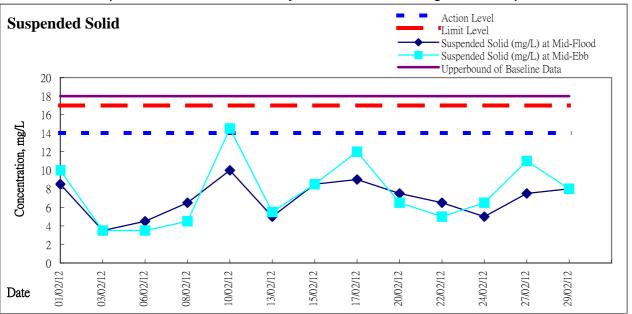

Remarks: WSD19 is located at upstream during the ebb tides while at downstream during flood tides.

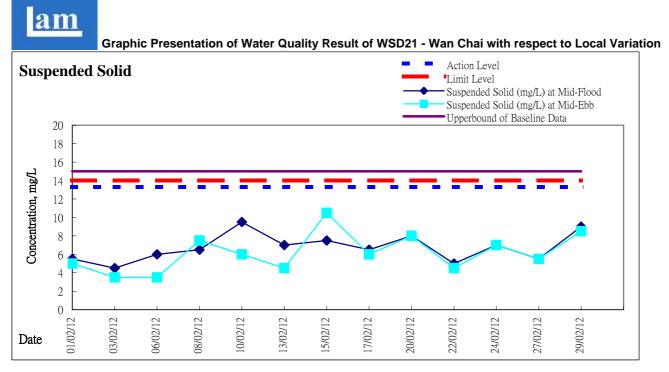

Remarks: WSD21 is located at upstream during the ebb tides while at downstream during flood tides.



Appendix 7.1

Construction Programme for Reporting Quarter

Activity ID	Activity Description	Orig Dur	Early Start	Late Start	Early Finish	Late Finish	Total Float	% Comp	p NOV	2011 DEC 5 12 19 26	JAN 2 9 16 23
	mation KT Cruise Terminal Develo	1	1		1	1	out	00m	P 28	<u>, 5 ,12 ,19 ,26</u>	<mark>_2 _9 16 2</mark> 3
Contract		•									
PD1100	Contract Period	1,486	30/11/09A	30/11/09A	24/12/13	24/12/13	0	4		Fenod	
	ccess/Vacate Date										
PV1020	Portion CA5b (Access)	0	29/02/12*	29/02/12*			0		0	 	
	aries & General Requirements						-			1	
Initial Subm											
SU1310	Material Submission of Bituminous & Road Marking	60	21/11/11	25/03/12	29/12/11	02/05/12	125	3	35		aterial Submission of Bituminous & Road Ma
	Accommodation										
TA1060	Servicing of Temp Accommodation for the Engineer	1,406	28/01/10A	28/01/10A	15/12/13	24/12/13	9	4	16 Servicing	of Temp Accommodation for the Engineer	
TA1070	Maintenance of Traffic Flow	1,344	28/02/10A	28/02/10A	14/11/13	24/12/13	40	4	16 Maintena		
Environmen	tal and Site Safety Monitoring										
ES1050	Monthly Update of SSP & EMP	1,422	07/12/09A	07/12/09A	09/11/13	24/12/13	45	4	19 Monthly C	Spitate of OOF & EMT	
ES1110	Impact Monitoring for Water Quality	1,380	05/02/10A	05/02/10A	27/11/13	24/12/13	27	4	7 impact M	onitoring for Water Quality	
ES1125	Maintenance of Silt Screen at WSD Intakes	1,380	31/01/10A	31/01/10A	22/11/13	24/12/13	32	4	7 Maintena	nce of Oilt Goreen at WOD Initiakes	
Mobilization	& Site Clearance										
MP1020	Routine Site Cleanliness and Tidiness	1,484	30/11/09A	30/11/09A	22/12/13	24/12/13	2	4	19 Fiourine C	ne ocanimess and rightess	
MP1060	Disposal of Surplus C&D Material	695	10/03/10A	10/03/10A	02/11/12	24/12/13	417	5	50 <mark>Disposai</mark>	of Surpius Out Material	
MP1070	Primary Sorting of C&D Material	1,200	26/03/10A	26/03/10A	19/07/13	24/12/13	158	4	19 <mark>Frimary S</mark>	borting of OQD Material	
MP1080	Surplus Rock Disposal in Area 1 & 2	700	15/02/11A	15/02/11A	24/03/13	24/12/13	275	3	30		
Sorting of C	&D Material				1						
SM1060	Bay F - Sorting and Mixing C&D Material	100	15/08/11A	15/08/11A	06/12/11	21/12/11	15	8	34	■■■■■■■■■■■■■■■■■■■■■■■■■■■■■■■■■■■■■	
SM1070	Bay G - Sorting and Mixing C&D Material	100	28/09/11A	28/09/11A	19/01/12	26/01/12	7	4	10		Bay G
SM1080	Bay H - Sorting and Mixing C&D Material	100		24/10/11A	10/03/12	09/05/12	60	1	0		
SM1090	Bay I - Sorting and Mixing C&D Material	100	14/11/11A	14/11/11A	22/03/12	09/05/12	48		0		
SM1100	Bay J - Sorting and Mixing C&D Material	100	26/12/11	03/02/12	03/04/12	12/05/12	39		0	Bay J - Sorting and Mixing C&D Material	
SM1110	Bay K - Sorting and Mixing C&D Material	100	26/12/11	12/08/12	03/04/12	19/11/12	230		0	Bay K - Sorting and Mixing C&D Material	
SM1120	Bay L - Sorting and Mixing C&D Material	100	16/12/11	21/12/12	24/03/12	30/03/13	371		0		
SM1130	Bay M - Sorting and Mixing C&D Material	100	26/12/11	05/09/12	03/04/12	13/12/12	254		0	Bay M - Sorting and Mixing C&D Material	
SM1150	PortionDZA -Sorting and Mixing C&D Material(toe)	400	12/03/11A		26/04/12	02/10/12	159				
SM1160	PortionDZB-Sorting and Mixing C&D Material(toe)	700	26/12/11	03/02/12	15/11/13	24/12/13	39		1 Port	tionDZB-Sorting and Mixing C&D Material(toe)	
Preparato	ory Works										
Production of	of Precast Units										
Precast Plank											
PW.4.1020	Deliver to Portion MQ2	0		25/12/13			683		0		
PW.4.1030	Deliver to Portion SDA	0	12/12/11	25/12/13			744		0	Deliver to Portion SDA	
	- Portion MQ1										
	(Bays A - B)									 	
New Seawall (70	07/10/11	07/10/11	11/10/11	00/05/10	1 40	-	70		vor (2050m2)
SW.1.4040	Bay A - Placing Scour Protection Layer (3250m3)	70		07/10/11A	11/12/11	02/05/12	143	/	70	Bay A - Placing Scour Protection La	yer (3230113)
SW.1.4090	Bay B - Placing Scour Protection Layer (3250m3)	70	21/11/11	23/02/12	29/01/12	02/05/12	94		0		
RC Deck Cons SW.1.5031	Bay A - Site Clearance	4	28/11/11	25/03/12	01/12/11	28/03/12	118		0	➡ Bay A - Site Clearance	
SW.1.5035	Bay A - Protective Coating	7	02/12/11	12/04/12	08/12/11	18/04/12	132		0	Bay A - Protective Coating	
SW.1.5040	Bay A - Dismantling Working Platform	14	09/12/11	19/04/12	22/12/11	02/05/12	132		0		tling Working Platform
SW.1.5070	Bay B - Precast Planks/Fix Rebar	14	21/11/11	08/03/12	04/12/11	21/03/12	102		0	Bay B - Precast Planks/Fix Rebar	
SW.1.5075	Bay B - RC Topping Concreting	7	05/12/11	22/03/12	11/12/11	28/03/12	108		0	△ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓ ✓	
SW.1.5075	Bay B - Site Clearance	4	12/12/11	08/04/12	15/12/11	11/04/12	118		0	Bay B - No repping contenting	
SW.1.5080	Bay B - Protective Coating	7	16/12/11	12/04/12	22/12/11	18/04/12	118		0	Bay B - Protect	ive Coating
SW.1.5085	Bay B - Dismantling Working Platform	14	23/12/11	19/04/12	05/01/12	02/05/12	118		0		Bay B - Dismantling Working Plat
SW.1.5090	Bay A - Construct Boundary Fence Wall	28	12/12/11	05/04/12	08/01/12	02/05/12	115		0	<u></u>	V Bay A - Construct Boundary
Miscellaneous						1				[· · · · · · · · · · · · · · · · · · ·
SW.1.6040	Installation of Navigation Light Post	21	21/11/11	12/04/12	11/12/11	02/05/12	143		0	VInstallation of Navigation Light Post	t
				и	L					·	·
				Ea	arly Bar	KTAP				Sheet 1 of	olan Balo
	PENTA-OCEAN			•	arget				Penta-O	cean Construction Co., Ltd.	Finish Date

Target

Progress Bar

Critical Activity



CEDD Contract No. KL/2009/01 Site Formation for Kai Tak Cruise Terminal Development Three Months Rolling Programme (Dec 2011- Feb 2012) Finish Date Data Date Run Date

	2012		
	FEB		MAR
23 <mark>30</mark>	6 ₁ 13 20	27	5
			1
			1
	Portion CA5t	o (Access) 🔶	
			1
Marking			ĺ
			1
			·
			1
G - Sorting and M	ixing C&D Material		
-			
			1
			1
			1
	Deliver to Portion MQ	2	i i
			·
VBa	B - Placing Scour Protection Layer (325	0m3)	
			1
			1
			1
			1
latform			
latform			
ary Fence Wall			
			1
30/11	09		
07/01	14 Date Revision	Checked	Approved
21/11	11 31/05/11 K	TM	WT
30/11/11 17			
		_	

Activity	Activity	Orig	Early	Late	Early	Late	Total	%	2011 2011 JAN JAN
ID	Description	Dur	Start	Start	Finish	Finish	Float Co	omp	^{np} 28 5 12 19 26 2 9 16 23
SW.1.6050	Flexible Surfacing	28	12/12/11	29/03/12	08/01/12	25/04/12	108	0	0 Flexible Surfacing
SW.1.6060	Road Marking	7	09/01/12	26/04/12	15/01/12	02/05/12	108	0	0 Contraction Cont
Section 2	- Portions MQ2, LS1, LS2, SDA & DZA								
Portion MQ2	(Bays C - G), LS1 & LS2								
Removal of Ex		1							
SW.2.3090	Bay G - Excavation Within MQ2 (22000m3)	35	26/09/11A	26/09/11A	04/12/11	24/11/11	-10	60	60 Bay G - Excavation Within MQ2 (22000m3)
New Seawall C									
SW.2.4060	Bay F - Filter 1 (2000m3)	11		24/11/11	03/12/11	04/12/11	1	0	0 Say F - Filter 1 (2000m3)
SW.2.4065	Bay F - Filter 2 (2000m3)	10	04/12/11	05/12/11	13/12/11	14/12/11	1	0	0 Bay F - Filter 2 (2000m3)
SW.2.4070	Bay F - Secondary Armour 0.16T ~ 0.25T (2500m3)	21	07/12/11	08/12/11	27/12/11	28/12/11	1	0	0 Bay F - Secondary Armour 0.16T ~ 0.25T (2500m3)
SW.2.4075	Bay F - Primary Armour 2.3T (1500m3)	21		22/12/11	10/01/12	11/01/12	1	0	0 Bay F - Primary Armour
SW.2.4080	Bay G - Filter 1 (2000m3)	14		25/11/11	18/12/11	08/12/11	-10	0	0 Bay G - Filter 1 (2000m3)
SW.2.4085	Bay G - Filter 2 (2000m3)	14	19/12/11	09/12/11	01/01/12	22/12/11	-10	0	0 Bay G - Filter 2 (2000m3)
SW.2.4090	Bay G - Secondary Armour 0.16T ~ 0.25T (2500m3)	21		23/12/11	22/01/12	12/01/12	-10	0	
SW.2.4095	Bay G - Primary Armour 2.3T (1500m3)	21	16/01/12	06/01/12	05/02/12	26/01/12	-10	0	0
SW.2.4100	Bay C to G -Scour Protection Layer (16250 m3)	240	21/11/11	06/02/12	17/07/12	02/10/12	77	0	0
RC Deck Cons		1							
SW.2.5005	Bay C - Formwork	30	05/11/11A		04/12/11	04/12/11	0	53	
SW.2.5010	Bay C - Rebar Fixing	30	05/12/11	05/12/11	03/01/12	03/01/12	0	0	0 Bay C - Rebar Fixing
SW.2.5015	Bay C - Corrosion Monitoring System	7	04/01/12	04/01/12	10/01/12	10/01/12	0	0	0 Bay C - Corrosion Mon
SW.2.5020	Bay C - Deck Beam Concreting	35	07/01/12	07/01/12	10/02/12	10/02/12	0	0	0
SW.2.5025	Bay C - Precast Planks/Fix Rebar	14	11/02/12	27/02/12	24/02/12	11/03/12	16	0	0
SW.2.5045	Bay D - Erection of Suspension Working Platform	28	21/11/11	07/11/11	18/12/11	04/12/11	-14	0	0 ■ ■ ■ ■ ■ ■ ■ ■ ■ ■ ■ ■ ■ ■ ■ ■ ■ ■ ■
SW.2.5050	Bay D - Formwork	30	19/12/11	05/12/11	17/01/12	03/01/12	-14	0	0 Bay D - Fo
SW.2.5055	Bay D - Rebar Fixing	30	04/01/12	21/12/11	02/02/12	19/01/12	-14	0	0
SW.2.5060	Bay D - Corrosion Monitoring System	7	03/02/12	20/01/12	09/02/12	26/01/12	-14	0	0
SW.2.5065	Bay D - Deck Beam Concreting	35	09/02/12	26/01/12	14/03/12	29/02/12	-14	0	0Ba
SW.2.5090	Bay E - Erection of Suspension Working Platform	28	19/12/11	04/12/11	15/01/12	31/12/11	-15	0	0 Bay E - Erection
SW.2.5095	Bay E - Formwork	30	16/01/12	01/01/12	14/02/12	30/01/12	-15	0	0
SW.2.5100	Bay E - Rebar Fixing	30	15/02/12	31/01/12	15/03/12	29/02/12	-15	0	0
SW.2.5135	Bay F - Erection of Suspension Working Platform	28	01/02/12	02/02/12	28/02/12	29/02/12	1	0	0 Bay F - Erection of Suspension Wor
SW.2.5180	Bay G - Erection of Suspension Working Platform	28	27/02/12	17/02/12	25/03/12	15/03/12	-10	0	0
Miscellaneous	Work								
SW.2.6010	Bay C - Utilities Trough/Sewerage Inside Deck	35	21/01/12	29/08/12	24/02/12	02/10/12	221	0	0 Bay C - Utilities Trough/Sewerage Inside Deck
SW.2.6012	Bay D - Utilities Trough/Sewerage Inside Deck	35	23/02/12	29/08/12	28/03/12	02/10/12	188	0	0
Portion SDA	(Bay SDA)								
New Seawall C	Construction								
SW.21.4080	Bay SDA - Scour Protection Layer (3950m3)	84	07/10/11A	07/10/11A	29/12/11	02/10/12	278	54	54 ▼Bay SDA - Scour Protection Layer (3950m3)
RC Deck Cons	truction	1			1	1			
SW.21.5040	Bay SDA (N)- Precast Planks/Fix Rebar	21	28/11/11	13/06/12	18/12/11	03/07/12	198	0	0 △ ───────────────────────────────────
SW.21.5050	Bay SDA (N)- RC Topping Concreting	35	19/12/11	04/07/12	22/01/12	07/08/12	198	0	0
SW.21.5060	Bay SDA (N)- Protective Coating Works	21	23/01/12	15/08/12	12/02/12	04/09/12	205	0	0
SW.21.5070	SDA(N)- Dismantle Soffit Platform & Bracing	28	13/02/12	05/09/12	11/03/12	02/10/12	205	0	0 SDA(N)-
SW.21.5110	Bay SDA (S)- Deck Beam Concreting	35	23/11/11A	23/11/11A	11/12/11	26/11/11	-15	40	40 Bay SDA (S)- Deck Beam Concreting
SW.21.5120	Bay SDA (S)- Precast Planks/Fix Rebar	21	12/12/11	13/06/12	01/01/12	03/07/12	184	0	0 ✓ Bay SDA (S)- Precast Planks/Fix Rebar
SW.21.5130	Bay SDA (S)- RC Topping Concreting	35	02/01/12	04/07/12	05/02/12	07/08/12	184	0	0
SW.21.5140	Bay SDA (S)- Protective Coating Works	21	06/02/12	15/08/12	26/02/12	04/09/12	191	0	0 Bay SDA (S)- Pr
SW.21.5150	SDA (S) Dismantle Soffit Platform & Bracing	28	27/02/12	05/09/12	25/03/12	02/10/12	191	0	0
Miscellaneous	Work			·					
SW.21.6010	Installation of Marine Fittings (Fender etc)	21	06/02/12	12/09/12	26/02/12	02/10/12	219	0	0 Installation of Mari
SW.21.6020	T&C of Corrision Monitoring System	7	06/02/12	26/09/12	12/02/12	02/10/12	233	0	0
SW.21.6030	Surface Drainage and Erection of Fencing	56	06/02/12	08/08/12	01/04/12	02/10/12	184	0	0 Surface Drainage a
Concret Block	Seawall			·		<u> </u>			
SW.21.7050	Insitu Copping for SB2-SB3	42	21/11/11	22/08/12	01/01/12	02/10/12	275	0	0 VInsitu Copping for SB2-SB3
	$PENTA-\Pi \Gamma EAN$			V Ea	arly Bar	KTAP			Sheet 2 of 4 Start Date
				=0		1		I	Penta-Ocean Construction Co., Ltd. Finish Date

Target

🔽 Progress Bar


Critical Activity



¹Start Date Finish Date Data Date Run Date

CEDD Contract No. KL/2009/01 Site Formation for Kai Tak Cruise Terminal Development Three Months Rolling Programme (Dec 2011- Feb 2012)

© Primavera Systems, Inc.

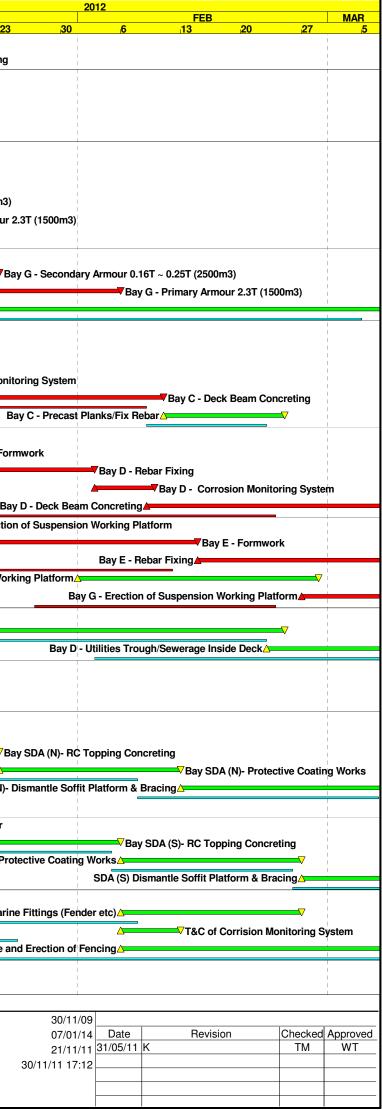

Activity ID	Activity Description	Orig Dur	Early Start	Late Start	Early Finish	Late Finish	Total Float	% Comp	NOV 28	2011 DEC 5 12 19 26	JAN 2 9 16 23
SW.21.7110	Insitu Copping for SB1	42	21/11/11	22/08/12	01/01/12	02/10/12	275	0	20		VInsitu Copping for SB1
Portion DZA										1	
Dredging Wor		1		1	1						
SW.22.1090	Remaining Area (264000 m3)	300	21/11/11	08/12/11	15/09/12	02/10/12	17	0			
Portion LS1											
Road & Drain SW.23.1000	age Works 600 Dia. Drainage Pipe	42	24/01/110	24/01/11A	11/12/11	06/02/12	57	50		✓600 Dia. Drainage Pipe	
SW.23.1000	Sewerage Pipe	42	24/01/11A	13/03/12	01/01/12	23/04/12	113	0			Sewerage Pipe
SW.23.1010	Fire Service Main	42	28/11/11	20/03/12	01/01/12	30/04/12	113	0		1	V Sewerage Fipe
SW.23.1020	Land Side Utility Trough	42	23/06/11A		12/01/12	10/06/12	150	6	_		✓ Land Side Utility Tro
SW.23.1040	Backfilling & Lay Sub-base	42	09/12/11	07/05/12	19/01/12	17/06/12	150	0		Δ	V Backfill
SW.23.1050	Road Base	42	16/12/11	14/05/12	26/01/12	24/06/12	150	0			
SW.23.1060	Base Course	42	23/12/11	21/05/12	02/02/12	01/07/12	150	0			
SW.23.1070	Wearing Course	42	30/12/11	28/05/12	09/02/12	08/07/12	150	0			
SW.23.1080	Road Marking	7	03/02/12	02/07/12	09/02/12	08/07/12	150	0			
SW.23.1090	Street Furniture & Lighting	35		11/06/12	16/02/12	15/07/12	150	0			Δ
Portion LS2					l					1	
Road & Drain	age Works										
SW.24.1000	600 Dia. Drainage Pipe	42	15/04/11A	15/04/11A	20/02/12	17/04/12	57	30		1	
SW.24.1010	Sewerage Pipe	42	03/10/11A	03/10/11A	26/02/12	23/04/12	57	2			
SW.24.1020	Fire Service Main	42	23/01/12	20/03/12	04/03/12	30/04/12	57	0			Fire Service Main
SW.24.1030	Land Side Utility Trough	42	30/01/12	18/07/12	11/03/12	28/08/12	170	0		1	Land Side Utili
SW.24.1040	Backfilling & Lay Sub-base	42	06/02/12	25/07/12	18/03/12	04/09/12	170	0			Back
SW.24.1050	Road Base	42	13/02/12	01/08/12	25/03/12	11/09/12	170	0			
SW.24.1060	Base Course	42	20/02/12	08/08/12	01/04/12	18/09/12	170	0			
SW.24.1070	Wearing Course	42	27/02/12	15/08/12	08/04/12	25/09/12	170	0		 	
Section 3	- Portion MQ3										
Portion MQ3	(Bays H - I)										
Piling Work											
Temp. Bracin SW.3.2605		21	14/11/110	14/11/11A	11/12/11	16/12/11	5			Bay H - Install Temp. Bracing & Sur	portinge
SW.3.2605	Bay H - Install Temp. Bracing & Supportings Bay I - Install Temp. Bracing & Supportings	21	23/11/11		13/12/11	16/12/11	3			VBay I - Install Temp. Bracing & Su	
	k & Removal of Existing Seawall	21	23/11/11	20/11/11	13/12/11	10/12/11	5	0			
SW.3.3010	Bay H-Remove Existing Seawall Rockfill (16500m3)	35	17/10/11A	17/10/11A	12/01/12	09/02/12	28	10			Bay H-Remove Exist
SW.3.3020	Bay H- Excavation Within MQ3 (22000m3)	35		21/10/11A	08/02/12	07/03/12	28	3		· · · · · · · · · · · · · · · · · · ·	
SW.3.3030	Bay H- Removal of Existing Abandoned Outfall	7	13/01/12		19/01/12		48	0			Bay H-
SW.3.3040	Bay I- Revmove Existing Seawall Armour (4500m3)	21		07/11/11A	02/01/12	05/01/12	3	4			Bay I- Revmove Existing Seawall Armou
SW.3.3050	Bay I-Remove Existing Seawall Rockfill (16500m3)	35	14/11/11A	14/11/11A	05/02/12	08/02/12	3	3			
SW.3.3060	Bay I- Excavation Within MQ3 (22000m3)	35	30/01/12	02/02/12	04/03/12	07/03/12	3	0			Bay I- Excavation Within MQ3 (
New Seawall	Construction										
SW.3.4000	Bay H - Filter 1 (2000m3)	11	09/02/12	22/03/12	19/02/12	01/04/12	42	0			
SW.3.4010	Bay H - Filter 2 (2000m3)	10	20/02/12	02/04/12	29/02/12	11/04/12	42	0			
SW.3.4020	Bay H - Secondary Armour 0.16T ~ 0.25T (2500m3)	21	23/02/12	05/04/12	14/03/12	25/04/12	42	0			
Section 4	- Portions MQ4, LS3, NDA & DZB									1	
Portion MQ4	(Bays J - M) & LS3										
Temp. Piling B	Bracing		1	1	1						
SW.4.2000	Bay J - Excavate Down to Bracing Level	14	21/11/11	30/12/11	04/12/11	12/01/12	39	0		Bay J - Excavate Down to Bracing Level	
SW.4.2005	Bay J - Install Pile Bracing	21	05/12/11	13/01/12	25/12/11	02/02/12	39	0		· · · · · · · · · · · · · · · · · · ·	stall Pile Bracing
SW.4.2010	Bay K - Excavate Down to Bracing Level	14	21/11/11	15/05/12	04/12/11	28/05/12	176	0		Bay K - Excavate Down to Bracing Level	
SW.4.2015	Bay K - Install Pile Bracing	21	05/12/11	29/05/12	25/12/11	18/06/12	176	0			stall Pile Bracing
SW.4.2020	Bay L - Excavate Down to Bracing Level	14	21/11/11	03/10/12	04/12/11	16/10/12	317	0		Bay L - Excavate Down to Bracing Level	
SW.4.2025	Bay L - Install Pile Bracing	21	25/11/11	07/10/12	15/12/11	27/10/12	317	0		Bay L - Install Pile Bracing	
SW.4.2030	Bay M - Excavate Down to Bracing Level	14	21/11/11	18/05/12	04/12/11	31/05/12	179	0		Variable Section Secti	
SW.4.2035	Bay M - Install Pile Bracing	21	05/12/11	01/06/12	25/12/11	21/06/12	179	0		∠ Bay M - Ir	nstall Pile Bracing

KTAP



Early Bar Penta-Ocean Construction Co., Ltd. Finish Date Target Data Date CEDD Contract No. KL/2009/01 Site Formation for Kai Tak Cruise Terminal Development Three Months Rolling Programme (Dec 2011- Feb 2012) Progress Bar Run Date Critical Activity

Sheet 3 of 4 Start Date

© Primavera Systems, Inc.

	2012	EED			MAR
23 <mark>,</mark> 30		FEB _13	20	27	MAR 5
					1
	- 				-
rough	 				
filling & Lay Sub	-base				
✓Road Ba	se				
	Base Cou	urse			1
		Wearing Course	•		
	Δ	Road Marking			
	 	 √Sti	reet Furnitu	ıre & Ligh	ting
				-	1
				ia. Draina	ge Pipe
		-		√Sew	erage Pipe
.					
tility Trough					
ackfilling & Lay S	ub-base				
	Ro	ad Base			
		Base Cours	eA		
	 	w	earing Cou	irse∆	
			-		
	1				
	' 				
isting Seawall Re	ockfill (16500r	m3)			
	 	Bay H- Excavatio	n Within M	Q3 (22000)m3)
H- Removal of Ex	isting Abando	oned Outfall			
nour (4500m3)	 				
	Bay	/ I-Remove Existing	Seawall Ro	ockfill (16	500m3)
3 (22000m3)		-			
					+
		Δ	Bay H -	Filter 1 (2	000m3)
	Вау	r H - Filter 2 (2000m3	B)		Y
Bay H - Se	condary Armo	our 0.16T ~ 0.25T (25	500m3) <u>/</u>	-	
				_	
					1
					1
	1				
30/11	/09	1			
07/01		Revision			Approved
	/11 31/05/11	ĸ		TM	WT
30/11/11 17	:12				

Activity	Activity	Orig	Early	Late	Early	Late	Total	%			2011 DEC						
ID	Description	Dur	Start	Start	Finish	Finish	Float	Comp 28		5	12	19	26	2	.9	<u>JAN</u> 16	23
Dredging Worl	k & Removal of Existing Seawall								I								· · · ·
SW.4.2900	Install Silt Curtain System (Bay J)	7	05/12/11	27/01/12	11/12/11	02/02/12	53	0		7	Install Silt	t Curtain S	ystem (Bay J)				
SW.4.2905	Install Silt Curtain System (Bay K)	7	05/12/11	12/06/12	11/12/11	18/06/12	190	0	Δ		Vinstall Silt	t Curtain S	ystem (Bay K)				
SW.4.2910	Install Silt Curtain System (Bay L)	7	25/11/11	21/10/12	01/12/11	27/10/12	331	0	✓Instal	II Silt Curta	in System (B	Bay L)					
SW.4.2915	Install Silt Curtain System (Bay M)	7	05/12/11	15/06/12	11/12/11	21/06/12	193	0		<i>t</i>	Install Silt	t Curtain S	ystem (Bay M)				
SW.4.3000	Bay J - Existing Seawall Armour (4500m3)	21	26/12/11	03/02/12	15/01/12	23/02/12	39	0					Δ			✓Bay J	- Existing
SW.4.3005	Bay J - Existing Seawall Rockfill (16500m3)	35	16/01/12	01/03/12	19/02/12	04/04/12	45	0					Bay J - Existing	g Seawa	II Rockfill (1650	00m3)	
SW.4.3010	Bay J - Excavation Within MQ4 (22000m3)	35	20/02/12	05/04/12	25/03/12	09/05/12	45	0									
SW.4.3015	Bay J - Remove Abandoned Submarine Outfall	7	20/02/12	03/05/12	26/02/12	09/05/12	73	0									
SW.4.3020	Bay K - Existing Seawall Armour (4500m3)	21	26/12/11	19/06/12	15/01/12	09/07/12	176	0					Δ			Bay K	- Existin
SW.4.3025	Bay K - Existing Seawall Rockfill (16500m3)	35	16/01/12	10/07/12	19/02/12	13/08/12	176	0	I				Bay K - Existinę	g Seawa	II Rockfill (1650	0m3)	
SW.4.3030	Bay K - Excavation Within MQ4 (22000m3)	35	20/02/12	14/08/12	25/03/12	17/09/12	176	0									
SW.4.3035	Bay K - Remove Abandoned Submarine Outfall	7	20/02/12	11/09/12	26/02/12	17/09/12	204	0									
SW.4.3040	Bay L - Existing Seawall Armour (4500m3)	21	16/12/11	28/10/12	05/01/12	17/11/12	317	0			Δ				Bay L - Exi	sting Seawall	Armour
SW.4.3045	Bay L - Existing Seawall Rockfill (16500m3)	35	06/01/12	18/11/12	09/02/12	22/12/12	317	0							Δ		
SW.4.3050	Bay L - Excavation Within MQ4 (22000m3)	35	10/02/12	23/12/12	15/03/12	26/01/13	317	0								Bay	y L - Exca
SW.4.3055	Bay L - Remove Abandoned Submarine Outfall	7	10/02/12	20/01/13	16/02/12	26/01/13	345	0	I I							Bay L -	Remove /
SW.4.3060	Bay M - Existing Seawall Armour (4800m3)	28	26/12/11	22/06/12	22/01/12	19/07/12	179	0					Δ				√Ba
SW.4.3065	Bay M - Existing Seawall Rockfill (20000m3)	42	23/01/12	20/07/12	04/03/12	30/08/12	179	0					Ва	iy M - Ex	isting Seawall	Rockfill (2000	0m3)/
Section 5	5 - Portion CA3, CA5B & WA1A			1	1	1	-1 1										
Transplantin	g and Tree Preservation																
LS1030	Preservation & Protection of Existing Trees	1,300	03/05/10A	03/05/10A	20/11/13	23/11/13	3	44									
	°			1	1	1											



Early Bar

Progress Bar

Critical Activity

Penta-Ocean Construction Co., Ltd.

CEDD Contract No. KL/2009/01 Site Formation for Kai Tak Cruise Terminal Development Three Months Rolling Programme (Dec 2011- Feb 2012) Sheet 4 of 4 Finish Date Data Date Run Date

	2012				
		FEB			MAR
2 <mark>3 30</mark>	6	₁ 13	20	27	5
	1			i.	
				1	
				1	
				l I	
				1	
				i.	
					_
ting Seawall Arı	nour (4500m3)				_
	()				
				1	
Bay J	- Excavation Within	n MQ4 (22000m	13)🛆		
Ray J - Ren	nove Abandoned S	ubmarine Outf			
Day 0 - Hell	nove Abanuoneu 3			I	
ting Seawall Ar	mour (4500m3)			i.	
				1	
			•	_	
Bay K	- Excavation Within	n MQ4 (22000m	13)		
Bay K - Ren	nove Abandoned S	ubmarine Outf	all		
-	I.				-
ur (4500m3)		,		1	
		Bay L - Existin	g Seawall	Rockfill (165	00m3)
veavation Within	MQ4 (22000m3)	-	-		
e Abandoned S	ubmarine Outfall 🛆			1	
Bay M - Evistir	g Seawall Armour	(4800m3)		i.	
	ig Seawaii Airii0ui			1	_
7					
	1			1	
				1	

30/11/09				
07/01/14	Date	Revision	Checked	Approved
21/11/11	31/05/11	К	ТМ	WT
30/11/11 17:12				
