



PROJECT NO.: TCS/00512/09

**DSD CONTRACT NO. DC/2009/13  
CONSTRUCTION OF SEWAGE TREATMENT WORKS AT  
YUNG SHUE WAN AND SOK KWU WAN**

**SOK KWU WAN PORTION AREA  
MONTHLY ENVIRONMENTAL MONITORING AND AUDIT  
(EM&A) REPORT (No.43) – FEBRUARY 2014**

PREPARED FOR  
**LEADER CIVIL ENGINEERING CORPORATION LIMITED**

**Quality Index**

<b>Date</b>	<b>Reference No.</b>	<b>Prepared By</b>	<b>Approved By</b>
24 March 2014	TCS00512/09/600/R0752v1		
		Martin Li Assistant Environmental Consultant	T.W. Tam Environmental Team Leader

<b>Version</b>	<b>Date</b>	<b>Description</b>
1	12 March 2014	First Submission
2	24 March 2014	Amended against IEC's comments on 24 March 2014

# URS CDM Joint Venture

---

Chief Engineer/Harbour Area Treatment Scheme  
Drainage Services Department  
5/F, Western Magistracy  
2A, Pok Fu Lam Road  
Hong Kong

Your reference:

Our reference: 05117/6/16/426154

Date: 25 Mar 2014

Attention: Mr Kenneth K W Kwong


**BY FAX**

Dear Madam

**Contract No. DC/2009/13**  
**Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan**  
**Sok Kwu Wan Portion Area**  
**Monthly Environmental Monitoring and Audit (EM&A) Report No. 43 (February 2014)**

We refer to the Monthly EM&A Monitoring Report No. 43 for February 2014 received under cover of the email from the Environmental Team, Action-United Environmental Services and Consulting (AUES), dated on 24 March 2014. We have no comment and have verified the captioned report.

Yours faithfully  
URS CDM JOINT VENTURE



Rodney Ip  
Independent Environmental Checker

ICWR/CKCH/lykl

Encl

cc	Leader Civil Engineering	(Attn: Mr Ron Hung)
	AUES	(Attn: Mr T.W. Tam)
	ER/LAMMA	(Attn: Mr Ian Jones)
	CDM	(Attn: Mr Sylvester Hsu)

## EXECUTIVE SUMMARY

ES.01. This is the 43<sup>th</sup> monthly Environmental Monitoring and Audit (EM&A) Report for Sok Kwu Wan (hereinafter ‘this Report’) for the designated works under the Environmental Permit [EP-281/2007/A], covering a period from **26 January 2014 to 25 February 2014** (hereinafter ‘the Reporting Period’).

### ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES.02. Environmental monitoring activities under the EM&A programme in this Reporting Period are summarized in the following table.

Issues	Environmental Monitoring Parameters / Inspection	Occasions
Air Quality	1-hour TSP	<b>54</b>
	24-hour TSP	<b>15</b>
Construction Noise	$L_{eq(30min)}$ Daytime	<b>20</b>
Water Quality	Marine Water Sampling	<b>12</b>
Inspection / Audit	ET Regular Environmental Site Inspection	<b>5</b>

ES.03. As informed by the Contractor, the marine work of outfall construction has been commenced on 19 July 2011, therefore, water quality was undertaken in this Reporting Period.

### BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES.04. No exceedance of air quality and construction noise monitoring were recorded in this Reporting Period. The statistics of environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

Environmental Issues	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Air Quality	1-hour TSP	0	0	0	--	--
	24-hour TSP	0	0	0	--	--
Construction Noise	$L_{eq(30min)}$ Daytime	0	0	0	--	--
Water Quality	DO	<b>0</b>	<b>0</b>	<b>0</b>	--	--
	Turbidity	<b>0</b>	<b>0</b>	<b>0</b>	--	--
	SS	<b>0</b>	<b>0</b>	<b>0</b>	--	--

Note: NOE – Notification of Exceedance

### SITE INSPECTION BY EXTERNAL PARTIES

ES.05. In this Reporting Period, weekly joint site inspection by RE, the Contractor and ET was carried out on **28 January and, 6, 11, 18 and 25 February 2014**. All the observation has been rectified in the set time frame.

### ENVIRONMENTAL COMPLAINT, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES.06. No written or verbal environmental complaint, summons or successful prosecutions were recorded in this Reporting Period.

### REPORTING CHANGE

ES.07. No reporting change was made in this Reporting Period.

### FUTURE KEY ISSUES

ES.08. During dry and windy season, the Contractor shall pay attention on the construction dust that may cause environmental issues in the upcoming months. Mitigation measures on construction dust

identified at the EM&A manual such as watering at haul road and covering of dusty material should be fully implemented.

- ES.09. Muddy water and other water quality pollutants via site surface water runoff into the sea body within Fish Culture Zone (FCZ) at Picnic Bay and the secondary recreation contact subzone at Mo Tat Wan is the key issue of the Project. Mitigation measures for water quality should be properly maintained to prevent any muddy or sandy runoff from the loose soil surface overflow on the site boundary.

## TABLE OF CONTENTS

<b>1</b>	<b>INTRODUCTION</b>	<b>1</b>
	PROJECT BACKGROUND	1
	REPORT STRUCTURE	2
<b>2</b>	<b>PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS</b>	<b>3</b>
	PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE	3
	CONSTRUCTION PROGRESS	3
	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	3
<b>3</b>	<b>SUMMARY OF BASELINE MONITORING REQUIREMENTS</b>	<b>4</b>
	ENVIRONMENTAL ASPECT	4
	MONITORING LOCATIONS	4
	MONITORING FREQUENCY AND PERIOD	5
	MONITORING EQUIPMENT	6
	EQUIPMENT CALIBRATION	9
	METEOROLOGICAL INFORMATION	9
	DATA MANAGEMENT AND DATA QA/QC CONTROL	9
	REPORTING	9
	DETERMINATION OF ACTION/LIMIT (A/L) LEVELS	9
<b>4</b>	<b>IMPACT MONITORING RESULTS - AIR QUALITY</b>	<b>11</b>
<b>5</b>	<b>IMPACT MONITORING RESULTS – CONSTRUCTION NOISE</b>	<b>12</b>
<b>6</b>	<b>IMPACT MONITORING RESULTS – WATER QUALITY</b>	<b>13</b>
<b>7</b>	<b>ECOLOGY</b>	<b>15</b>
<b>8</b>	<b>WASTE MANAGEMENT</b>	<b>16</b>
<b>9</b>	<b>SITE INSPECTION</b>	<b>17</b>
<b>10</b>	<b>ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE</b>	<b>18</b>
<b>11</b>	<b>IMPLEMENTATION STATUS OF MITIGATION MEASURES</b>	<b>19</b>
<b>12</b>	<b>IMPACT FORECAST</b>	<b>25</b>
<b>13</b>	<b>CONCLUSIONS AND RECOMMENDATIONS</b>	<b>26</b>
	CONCLUSIONS	26
	RECOMMENDATIONS	26

## **LIST OF TABLES**

Table 2-1	Status of Environmental Licenses and Permits
Table 3-1	Summary of EM&A Requirements
Table 3-2	Location of Air Quality Monitoring Station
Table 3-3	Location of Construction Noise Monitoring Station
Table 3-4	Location of Marine Water Quality Monitoring Station
Table 3-5	Action and Limit Levels for Air Quality
Table 3-6	Action and Limit Levels for Construction Noise
Table 3-7	Action and Limit Levels for Marine Water Quality
Table 4-1	Summary of 24-hour and 1-hour TSP Monitoring Results – AM1
Table 4-2	Summary of 24-hour and 1-hour TSP Monitoring Results – AM2
Table 4-3	Summary of 24-hour and 1-hour TSP Monitoring Results – AM3
Table 5-1	Summarized of Construction Noise Monitoring Results at NM1
Table 5-2	Summarized of Construction Noise Monitoring Results at NM2
Table 5-3	Summarized of Construction Noise Monitoring Results at RNM3
Table 5-4	Summarized of Construction Noise Monitoring Results at NM4
Table 6-1	Summary of Water Quality Results – Mid-ebb Tides (Dissolved Oxygen)
Table 6-2	Summary of Water Quality Results – Mid-ebb Tides (Turbidity & Suspended Solids)
Table 6-3	Summary of Water Quality Results – Mid-flood Tides (Dissolved Oxygen)
Table 6-4	Summary of Water Quality Results – Mid-flood Tides (Turbidity & Suspended Solids)
Table 6-5	Summarized Exceedances of Marine Water Quality
Table 8-1	Summary of Quantities of Inert C&D Materials
Table 8-2	Summary of Quantities of C&D Wastes
Table 8-1	Site Observations
Table 10-1	Statistical Summary of Environmental Complaints
Table 10-2	Statistical Summary of Environmental Summons
Table 10-3	Statistical Summary of Environmental Prosecution
Table 11-1	Environmental Mitigation Measures

## **LIST OF APPENDICES**

Appendix A	Site Layout Plan – Sok Kwu Wan Portion Area
Appendix B	Organization Structure and Contact Details of Relevant Parties
Appendix C	Three Months Rolling Construction Programme
Appendix D	Location of Monitoring Stations (Air Quality / Construction Noise / Water Quality)
Appendix E	Monitoring Equipments Calibration Certificate
Appendix F	Event and Action Plan
Appendix G	Impact Monitoring Schedule
Appendix H	Monitoring Data Sheet
Appendix I	Graphical Plots of Monitoring Results
Appendix J	Meteorological Information
Appendix K	Monthly Summary Waste Flow Table
Appendix L	Weekly Site Inspection Checklist
Appendix M	Implementation Schedule of Mitigation Measures
Appendix N	Tree Inspection Report

## 1 INTRODUCTION

### PROJECT BACKGROUND

- 1.01 The Leader Civil Engineering Corporation Limited (Leader) has been awarded the *Contract DC/2009/13 - Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan* (the Project) by the Drainage Services Department (DSD) on 4 May 2010. The Project is part of an overall plan approved under a statutory EIA for Outlying Islands Sewerage Stage 1 Phase 2 Package J – Sok Kwu Wan Sewage Collection and Treatment (Register No. AEIAR-075/2003) and Disposal Facilities and Outlying Islands Sewerage Stage 1 Phase 1 Package C – Yung Shue Wan Sewage Treatment Works and Outfall (Register No. EIA-124/BC). The Environmental Permit (EP) No. EP-281/2007 and EP-282/2007 for the Project have been obtained by the DSD on 29 June 2007 for the relevant works. After July 2009, EP-281/2007/A instead EP-281/2007 is EP for Sok Kwu Wan relevant works.
- 1.02 The Project involves construction of sewage treatment works at Sok Kwu Wan and Yung She Wan with a capacity of 1,430m<sup>3</sup>/day and 2,850m<sup>3</sup>/day respectively to provide secondary treatment, construction of 2 pumping stations at Sok Kwu Wan and 1 pumping station at Yung Shue Wan, construction of submarine outfall from the coastline and laying of underground sewerage pipeline. The site layout plan for the captioned work under the Project is showing in **Appendix A**.
- 1.03 According to the Particular Specification (PS) and **Appendix 25** of the Project, Leader should establish an Environmental Team (ET) to implement the environmental monitoring and auditing works to fulfill the requirements as stipulated in the Environmental Monitoring and Audit (EM&A) Manual. This EM&A Manual is referred to the Appendix B of the Review Report on EIA Study – Sok Kwu Wan (Final) in January 2007 (Agreement No. CE 20/2005(DS)).
- 1.04 Action-United Environmental Services and Consulting (AUES) has been commissioned by Leader as the ET to implement the relevant EM&A programme. Organization chart of the Environmental Team for the Project is shown in **Appendix B**. For ease of reporting, the proposed EM&A programme for baseline and impact monitoring is split to following two stand-alone parts:
- (a) Proposed EM&A Programme for Baseline and Impact Monitoring – Sok Kwu Wan (under EP No. 281/2007/A varied on 23 September 2009)
  - (b) Proposed EM&A Programme for Baseline and Impact Monitoring – Yung Shue Wan (under EP No. 282/2007)
- 1.05 According to the EM&A Manual of Sok Kwu Wan and Yung Shue Wan, baseline water quality monitoring should be carried out for consecutive six months before the marine work commencement. Therefore, the baseline reports of Sok Kwu Wan and Yung Shue Wan are divided to two volumes i.e. the Volume 1 for air quality and noise monitoring; and the Volume II for water quality monitoring for separate submission.
- 1.06 There is a concurrent DSD contract “*DC/2007/18 Yung Shue Wan and Sok Kwu Wan Village Sewerage, Stage 1 Works*” undertaking at Sok Kwu Wan since April 2008.
- 1.07 Consider that the construction works of DC/2007/18 and DC/2009/13 at Sok Kwu Wan is under the same Environmental Permit and EM&A Manual, the performance criteria of air quality and construction noise at Sok Kwu Wan under the Project is recommended to adopt the Action/Limit Levels established by contract DC/2007/18. The Baseline Monitoring Report Volume 1 under the Project for air quality and noise at Sok Kwu Wan was submitted on 9 July 2010 and verified by IEC and for EPD endorsement before the relevant land works commencement on 27 July 2010.
- 1.08 This is the **43<sup>rd</sup>** monthly EM&A Report – Sok Kwu Wan Portion Area presenting the monitoring results and inspection findings for the Reporting Period from **26 January 2014 to 25 February 2014**.

---

**REPORT STRUCTURE**

1.09 The Monthly Environmental Monitoring and Audit (EM&A) Report – Sok Kwu Wan is structured into the following sections:-

<b>SECTION 1</b>	<b>INTRODUCTION</b>
<b>SECTION 2</b>	<b>PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS</b>
<b>SECTION 3</b>	<b>SUMMARY OF MONITORING REQUIREMENTS</b>
<b>SECTION 4</b>	<b>AIR QUALITY MONITORING RESULTS</b>
<b>SECTION 5</b>	<b>CONSTRUCTION NOISE MONITORING RESULTS</b>
<b>SECTION 6</b>	<b>WATER QUALITY MONITORING RESULTS</b>
<b>SECTION 7</b>	<b>WASTE MANAGEMENT</b>
<b>SECTION 8</b>	<b>SITE INSPECTIONS</b>
<b>SECTION 9</b>	<b>ENVIRONMENTAL COMPLAINTS AND NON-COMPLIANCE</b>
<b>SECTION 10</b>	<b>IMPLEMENTATION STATUES OF MITIGATION MEASURES</b>
<b>SECTION 11</b>	<b>IMPACT FORECAST</b>
<b>SECTION 12</b>	<b>CONCLUSIONS AND RECOMMENDATION</b>



## 2 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

### PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE

- 2.01 Organization structure and contact details of relevant parties with respect to on-site environmental management are shown in [Appendix B](#).

### CONSTRUCTION PROGRESS

- 2.02 The three month rolling construction programme are enclosed in [Appendix C](#) and the major construction activities undertaken in this Reporting Period are listed below:-
- Excavation for utilities construction under EVA in SKWSTW
  - Soil nailing in SKWSTW
  - Finishing works in SKWSTW & PS2
  - E&M installation in SKWSTW & PS2

### SUMMARY OF ENVIRONMENTAL SUBMISSIONS

- 2.03 Summary of the relevant permits, licences, and/or notifications on environmental protection for this Project in this Reporting Period is presented in [Table 2-1](#).

**Table 2-1 Status of Environmental Licenses and Permits**

Item	Description	License/Permit Status
1	Air Pollution Control (Construction Dust) Regulation	Notified EPD on 19 May 2010 Ref.: 317486
2	Chemical Waste Producer Registration	Issued on 8/6/2010 WPN 5213-912-L2720-01
3	Water Pollution Control Ordinance	Approved on 29/9/2010 Valid to: 30/09/2015 Licence no.: WT00007567-2010
4	Billing Account for Disposal of Construction Waste	Issued on 26 May 2010 A/C No: 7010815

- 2.04 The “Baseline/Impact Monitoring Methodology (TCS00512/09/600/R0010Ver.4)” was set out in accordance with the Sok Kwu Wan EM&A Manual’ requirements. It was approved by the Engineer Representative (ER) and agreed with the Independent Environmental Checker (IEC) and then submitted to the EPD on 8 July 2010.
- 2.05 Baseline Monitoring Report - Volume 1 for Sok Kwu Wan (TCS00512/09/600/R0020Ver.3) was verified by the IEC on 12 July 2010 and submitted to EPD on 12 July 2010.
- 2.06 Baseline Water Quality Monitoring Report - Volume 2 for Sok Kwu Wan (TCS00512/09/600/R0182v7) was revised against EPD comments and re-submitted on 11 October 2011.

### 3 SUMMARY OF BASELINE MONITORING REQUIREMENTS

#### ENVIRONMENTAL ASPECT

- 3.01 The EM&A baseline monitoring programme cover the following environmental issues:
- Air quality;
  - Construction noise; and
  - Marine water quality
- 3.02 The ET implements the EM&A programme in accordance with the aforementioned requirements. Detailed air quality, construction noise and water quality of the EM&A programme are presented in the following sub-sections.
- 3.03 A summary monitoring parameters for the air quality, noise and marine water monitoring is presented in *Table 3-1*:

**Table 3-1 Summary of EM&A Requirements**

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> <li>• 1-hour TSP Monitoring by Real-Time Portable Dust Meter; and</li> <li>• 24-hour TSP Monitoring by High Volume Air Sampler.</li> </ul>
Noise	<ul style="list-style-type: none"> <li>• Leq (30min) during normal working hours; and</li> <li>• Leq (15min) during Restricted Hours.</li> </ul>
Marine Water Quality	<p><b><i>In-situ Measurements</i></b></p> <ul style="list-style-type: none"> <li>• Dissolved Oxygen Concentration (DO) (mg/L);</li> <li>• Dissolved Oxygen Saturation (%);</li> <li>• Turbidity (NTU);</li> <li>• pH unit;</li> <li>• Salinity (ppt);</li> <li>• Water depth (m); and</li> <li>• Temperature (°C).</li> </ul> <p><b><i>Laboratory Analysis</i></b></p> <ul style="list-style-type: none"> <li>• Suspended Solids (SS) (mg/L)</li> </ul>

#### MONITORING LOCATIONS

##### Air Quality

- 3.04 Three air monitoring stations: AM1, AM2 and AM3 were designated in the *EM&A Manual Section 2.5*. The detailed air monitoring stations is described in *Table 3-2* and graphical is shown in *Appendix D*.

**Table 3-2 Location of Air Quality Monitoring Station**

Sensitive Receiver	Location
AM1	Squatter house in Chung Mei Village
AM2	Squatter house in Chung Mei Village
AM3	Football court

##### Construction Noise

- 3.05 According to *EM&A Manual Section 3.4*, there were four noise sensitive receivers (NM1-NM4) designated for the construction noise monitoring. NM1, NM2 and NM4 of the three designated monitoring stations were identified and are monitored by the current DSD contract DC/2007/18. However, the premises monitoring station NM3 was rejected by the owner of 1B Sok Kwu Wan and an alternative noise monitoring station RNM3 replacement was proposed by the contract DC/2007/18 ET and accepted by the IEC and EPD before the baseline monitoring commencement in April 2008. The location RNM3 is located at Sok Kwu Wan Sitting-out area which just 3m width footpath away from the original location house 1B. The detailed construction noise monitoring stations to also under the Project is described in *Table 3-3* and graphical is shown in *Appendix D*.

**Table 3-3 Location of Construction Noise Monitoring Station**

Sensitive Receiver	Location
NM1	1, Chung Mei Village
NM2	20, Sok Kwu Wan
RNM3	Sok Kwu Wan Sitting-out Area
NM4	2-storey village house at Ta Shui Wan

### Water Quality

- 3.06 Three control stations (C1-C3) and three impact stations (W1-W3) were recommended in the *EM&A Manual Section 4.5*. Impact stations W1-W3 identified at the sensitive receivers (FCZ and secondary contact recreation subzone) to monitor the impacts from the construction of the submarine outfall as well as the effluent discharge from the proposed STW on water quality. Three control stations: C1, C2 & C3 were specified at locations representative of the project site in its undisturbed condition and located at upstream and downstream of the works area. Detailed and co-ordination of marine water quality monitoring stations is described in **Table 3-4** and the graphical is shown in **Appendix D** and would be performed for EM&A programme.

**Table 3-4 Location of Marine Water Quality Monitoring Station**

Station	Description	Co-ordination	
		Easting	Northing
W1	Secondary recreation contact subzone at Mo Tat Wan	832 968	807 732
W2	Fish culture zone at Picnic Bay	832 670	807 985
W3	Fish culture zone at Picnic Bay	832 045	807 893
C1 (flood)	Control Station	833 703	808 172
C2	Control Station	831 467	807 747
C3 (ebb)	Control Station	832 220	808 862

### **MONITORING FREQUENCY AND PERIOD**

- 3.07 The impact monitoring carried out in the EM&A programme is basically in accordance with the requirements in *EM&A Manual Sections 2.7, 3.6, 4.7 and 4.8*. The monitoring requirements are listed as follows.

#### Air Quality Monitoring

Parameters: 1-hour TSP and 24-hour TSP.

Frequency: Once in every six days for 24-hour TSP and three times in every six days for 1-hour TSP.

Duration: Throughout the construction period.

#### Noise Monitoring

Parameters:  $L_{eq(30min)}$  &  $L_{eq(5min)}$ ,  $L_{10}$  and  $L_{90}$ .  
 $L_{eq(15min)}$  &  $L_{eq(5min)}$ ,  $L_{10}$  and  $L_{90}$  during the construction undertaken during Restricted hours (19:00 to 07:00 hours next of normal working day and full day of public holiday and Sunday)

Frequency: Once per week during 0700-1900 hours on normal weekdays. Restricted hour monitoring should depend on conditions stipulated in Construction Noise Permit.

Duration: Throughout the construction period.

#### Marine Water Quality Monitoring

Parameters: Duplicate in-situ measurements: water depth, temperature, dissolved oxygen, pH, turbidity and salinity;  
HOKLAS-accredited laboratory analysis: suspended solids

- Frequency: Three days a week, at mid ebb and mid flood tides. The interval between 2 sets of monitoring will be more than 36 hours.
- Sampling Depth
- (i.) Three depths: 1m below water surface, 1m above sea bottom and at mid-depth when the water depth exceeds 6m.
  - (ii.) If the water depth is between 3m and 6m, two depths: 1m below water surface and 1m above sea bottom.
  - (iii.) If the water depth is less than 3m, 1 sample at mid-depth is taken
- Duration: During the course of marine works

### **Post-Construction Monitoring – Marine Water**

- 3.08 Upon the marine works (dredging and HDD pipe installation) completion, 4 weeks of post-construction monitoring would be undertaken in accordance with the *Section 4.8 of EM&A Manual*. The requirements of post-construction monitoring such as the parameter, frequency, location and sampling depth is same as the impact monitoring.

### **MONITORING EQUIPMENT**

#### Air Quality Monitoring

- 3.09 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If the ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to the IEC to approve. The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.

#### 1-hour TSP

- 3.10 The 1-hour TSP monitor, a TSI Dust Track Aerosol Monitor Model 8520 or Sibata LD-3 Laser Dust Meter is a portable, battery-operated laser photometer. The 1-hour TSP meter provides a real time 1-hour TSP measurement based on 90° light scattering. The 1-hour TSP monitor consisted of the following:
- a. A pump to draw sample aerosol through the optic chamber where TSP is measured;
  - b. A sheath air system to isolate the aerosol in the chamber to keep the optics clean for maximum reliability; and
  - c. A built-in data logger compatible with Windows based program to facilitate data collection, analysis and reporting.

#### 24-hour TSP

- 3.11 The equipment used for 24-hour TSP measurement will be a TISCH High Volume Air Sampler, HVS Model TE-5170, which complied with EPA Code of Federal Regulation, Appendix B to Part 50. The HVS consists of the following:
- a. An anodized aluminum shelter;
  - b. A 8"x10" stainless steel filter holder;
  - c. A blower motor assembly;
  - d. A continuous flow/pressure recorder;
  - e. A motor speed-voltage control/elapsed time indicator;
  - f. A 7-day mechanical timer, and
  - g. A power supply of 220v/50 hz
- 3.12 For HVS for 24-hour TSP monitoring, the HVS is mounted in a metallic cage with a top for protection and also it is sat on the existing ground. The flow rate of the HVS between 0.63m<sup>3</sup>/min and 1.7m<sup>3</sup>/min will be properly set in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50. Glass Fiber Filter 8" x 10" of TE-653 will be used for 24-hour TSP monitoring and would be supplied by laboratory. The general procedures of sampling are described as below:-
- A horizontal platform with appropriate support to secure the samples against gusty wind should be provided;

- No two samplers should be placed less than 2 meters apart;
  - The distance between the sampler and an obstacle, such as building, must be at least twice the height that the obstacle protrudes above the sample;
  - A minimum of 2 meters of separation from any supporting structure, measured horizontally is required;
  - Before placing any filter media at the HVS, the power supply will be checked to ensure the sampler work properly;
  - The filter paper will be set to align on the screen of HVS to ensure that the gasket formed an air tight seal on the outer edges of the filter. Then filter holder frame will be tightened to the filter hold with swing bolts. The holding pressure should be sufficient to avoid air leakage at the edge.
  - The mechanical timer will be set for a sampling period of 24 hours (00:00 mid-night to 00:00 mid-night next day). Information will be recorded on the field data sheet, which would be included the sampling data, starting time, the weather condition at current and the filter paper ID with the initial weight;
  - After sampling, the filter paper will be collected to transfer from the filter holder of the HVS to a sealed in the envelope and sent to a local HOKLAS accredited laboratory for quantifying.
- 3.13 All the sampled 24-hour TSP filters will be kept in normal air conditioned room conditions, i.e. 70% HR (Relative Humidity) and 25°C, for six months prior to disposal.
- 3.14 The HVS used for 24-hour TSP monitoring will be calibrated before the commencement for sampling, and after in two months interval for 1 point checking of maintenance and six months interval for five points calibrate in accordance with the manufacturer's instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5028A) to establish a relationship between the follow recorder meter reading in cfm (cubic feet per minute) and the standard flow rate, Qstd, in m<sup>3</sup>/min.
- Noise Monitoring
- 3.15 Sound level meter in compliance with the *International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1)* specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m s<sup>-1</sup>.
- 3.16 All noise measurements will be performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq). Leq(30 min) in six consecutive Leq(5 min) measurements will be used as the monitoring parameter for the time period between 0700-1900 hours on weekdays throughout the construction period. Leq(15 min) in three consecutive Leq(5 min) measurements for other time periods (e.g. during restricted hours) will only be conducted for monitoring the construction noise during restricted hours as necessary.
- 3.17 The sound level meter will be mounted on a tripod at a height of 1.2 m and placed at the assessment point and oriented such that the microphone is pointed to the site with the microphone facing perpendicular to the line of sight. The windshield will be fitted for all measurements. Where a measurement is to be carried out at a building, the assessment point would normally be at a position 1 m from the exterior of the building façade. Where a measurement is to be made for noise being received at a place other than a building, the assessment point would be at a position 1.2 m above the ground in a free-field situation, i.e. at least 3.5 m away from reflective surfaces such as adjacent buildings or walls.
- 3.18 Immediately prior to and following each noise measurement the accuracy of the sound level meter will be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements will be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0dB.
- 3.19 Noise measurements will not be made in fog, rain, wind with a steady speed exceeding 5m/s or

wind with gusts exceeding 10m/s. The wind speed will be checked with a portable wind speed meter capable of measuring the wind speed in m/s. An acoustic calibrator and sound level meter will be calibrated yearly. A valid of Calibration certificates will be shown in the Environmental Monitoring Report accordingly.

#### Water Quality Monitoring

- 3.20 Marine water quality monitoring will be conducted at the designated locations in accordance with EM&A Manual. The operating and analytical of sampling procedures are described as below:
- A Global Positioning System (GPS) will be used to ensure that the correct location was selected prior to sample collection. A portable, battery-operated echo sounder will be used for the determination of water depth at each designated monitoring station.
  - The marine water sampler will be lowered into the water body at a predetermined depth. The trigger system of the sampler is activated with a messenger and opening ends of the sampler are closed accordingly then the sample of water is collected.
  - During the sampling, the sampling container will be rinsed to use a portion of the marine water sample before the water sample is transferred to the container. Upon sampling completion, the container is sealed with a screw cap.
  - Before the sampling process, general information such as the date and time of sampling, weather condition and tidal condition as well as the personnel responsible for the monitoring will be recorded on the monitoring field data sheet.
  - In-situ measurement including water temperature, turbidity, dissolved oxygen, salinity, pH and water depth undertake at the identified monitoring point. At each station, marine water samples are collected at three depths: 1m below water surface, 1m above sea bottom and at mid-depth when the water depth exceeds 6m. Samples at 1m below water surface and 1m above sea bottom are collected when the water depth is between 3m and 6m. Only 1 sample at mid-depth is taken when the water depth is below 3m.
  - For the in-situ measurement, two consecutive measurements of sampling depth, temperature, dissolved oxygen, salinity, turbidity and pH concentration will be measured at the sea. The YSI Model 6820 Multi-parameter Water Quality Sonde is retrieved out of the water after the first measurement and then re-deployed for the second measurement. Where the difference in the value between the first and second readings of each set is more than 25% of the value of the first reading, the reading is discarded and further readings is taken.
  - Water sample collection would be used the water sampler. During the water sample collected from the sea, it is fill in high-density polythene bottles. Before the water sample storage, the sampling bottles will be pre-rinsed with the same water sample. The sample bottles then is packed in cool-boxes (cooled at 4°C without being frozen), and delivered to HOKLAS accredited laboratory for the chemical analysis as followed APHA *Standard Methods for the Examination of Water and Wastewater* 19ed 2540D, unless otherwise specified.
  - The laboratory has be comprehensive quality assurance and quality control programmes. For QA/QC procedures, one duplicate samples of every batch of 20 samples is analyzed as followed the HOKLAS accredited requirement.
- 3.21 For the marine water sampling period, the Multi-parameter Water Quality Monitoring System will be calibrated by three month interval accordingly. The available calibration certificate will be issued to ensure the performance of Multi-parameter Water Quality Monitoring System to use for in-situ measurement.
- 3.22 All water samples will be analyzed with various chemical tests as specified in the EM&A Manual by a local HOKLAS-accredited testing laboratory (ALS Technichem (HK) Pty Ltd HOKLAS registration no. 66). Duplicate samples from each independent sampling event are required for all parameters and the samples will be mixed and analyzed in one set of laboratory analysis. The mixed process would be carried by the laboratory. The determination works should start within 24 hours after collection of the water samples or within the holding time as advised by the laboratory. The laboratory analysis result will be input in our computer database upon received from the laboratory.

### EQUIPMENT CALIBRATION

- 3.23 Calibration of the HVS is performed upon installation in accordance with the manufacturer's instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5025A). The calibration data are properly documented and the records are maintained by ET for future reference.
- 3.24 The 1-hour TSP meter was calibrated by the supplier prior to purchase. Zero response of the equipment was checked before and after each monitoring event. In-house calibration with the High Volume Sampler (HVS) in same condition was undertaken in yearly basis.
- 3.25 The sound level meter and calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis.
- 3.26 The Multi-parameter Water Quality Monitoring System will be calibrated by HOKLAS accredited laboratory of three month intervals. The available calibration certificate will be issued to ensure the performance of Multi-parameter Water Quality Monitoring System to use for in-situ measurement.
- 3.27 All updated calibration certificates of the monitoring equipment used for the impact monitoring programme in the Reporting Period would be attached in [Appendix E](#).

### METEOROLOGICAL INFORMATION

- 3.28 The meteorological information during the construction phase is obtained from the Wong Chuk Hang Station of the Hong Kong Observatory (HKO) due to it nearly the Project site.

### DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.29 The impact monitoring data are handled by the ET's systematic data recording and management, which complies with in-house Quality Management System. Standard Field Data Sheets (FDS) are used in the impact monitoring programme.
- 3.30 The monitoring data recorded in the equipment e.g. 1-hour TSP meter, sound level meter and Multi-parameter Water Quality Monitoring System, are downloaded directly from the equipments at the end of each monitoring day. The downloaded monitoring data are input into a computerized database properly maintained by the ET. The laboratory results are input directly into the computerized database and QA/QC checked by personnel other than those who input the data. For monitoring activities require laboratory analysis, the local laboratory follows the QA/QC requirements as set out under the HOKLAS scheme for all laboratory testing.

### REPORTING

- 3.31 It was agreed among the ER, IEC, Contractor and ET that, in order to streamline the EM&A report submission and to cater for the occasional delay in obtaining laboratory analysis results, the cutoff day for each month is the 25<sup>th</sup> i.e. the first day of each report is the 26<sup>th</sup> of the last month and the end day, the 25<sup>th</sup> of that month.

### DETERMINATION OF ACTION/LIMIT (A/L) LEVELS

- 3.32 According to the Sok Kwu Wan Environmental Monitoring and Audit Manual, the air quality, construction noise and marine water quality were set up, namely Action and Limit levels are listed in [Tables 3-5, 3-6 and 3-7](#) as below.

**Table 3-5 Action and Limit Levels for Air Quality**

Monitoring Station	Action Level ( $\mu\text{g}/\text{m}^3$ )		Limit Level ( $\mu\text{g}/\text{m}^3$ )	
	1-hour	24-hour	1-hour	24-hour
AM1	343	173	500	260
AM2	331	175	500	260
AM3	353	191	500	260

**Table 3-6 Action and Limit Levels for Construction Noise**

Monitoring Location	Action Level	Limit Level
	0700-1900 hours on normal weekdays	
NM1 NM2 RNM3 NM4	When one or more documented complaints are received	75 dB(A) of $L_{eq(30min)}$ during normal hours from 0700 to 1900 hours on normal weekdays, reduced to 70 dB(A) of $L_{eq(30min)}$ for schools and 65 dB(A) during school examination periods

**Table 3-7 Action and Limit Levels for Marine Water Quality**

Parameter	Performance Criteria	Impact Station		
		W1	W2	W3
DO Concentration (Surface and Middle) (mg/L)	Action Level	5.39	4.64	4.71
	Limit Level	5.29	4.56	4.54
DO Concentration (Bottom) (mg/L)	Action Level	N/A	3.60	3.37
	Limit Level	N/A	3.06	3.18
Turbidity (Depth-Average) (NTU)	Action Level	4.39	4.84	6.48
	Limit Level	6.06	5.99	6.71
Suspended Solids (Depth-Average) (mg/L)	Action Level	12.41	9.24	10.79
	Limit Level	12.68	11.28	12.25

- 3.33 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan enclosed in [Appendix F](#).



#### 4 IMPACT MONITORING RESULTS - AIR QUALITY

4.01 The impact EM&A programme was carried out as compliance with the contract Particular Specification, Sok Kwu Wan EM&A Manual and the EP. The impact monitoring schedule for the Reporting Period and next Reporting Period is presented in [Appendix G](#).

##### Results of Air Quality Monitoring

4.02 In this Reporting Period, **54** and **15** monitoring events were performed for 1-hour TSP and 24-hour TSP monitoring respectively at the designated locations AM1, AM2 and AM3. The monitoring results for 24-hour and 1-hour TSP are summarized in [Tables 4-1, 4-2](#) and [4-3](#). The detail 24-hour TSP data are shown in [Appendix H](#) and the graphical plots of are shown in [Appendix I](#).

**Table 4-1 Summary of 24-hour and 1-hour TSP Monitoring Results – AM1**

Date	24-hour TSP ( $\mu\text{g}/\text{m}^3$ )	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )				
		Date	Start Time	1 <sup>st</sup> hour measured	2 <sup>nd</sup> hour measured	3 <sup>rd</sup> hour measured
27-Jan-14	58	28-Jan-14	11:51	92	96	88
4-Feb-14	22	5-Feb-14	11:28	15	22	28
10-Feb-14	61	8-Feb-14	11:24	43	62	69
15-Feb-14	29	12-Feb-14	12:42	123	141	149
21-Feb-14	47	18-Feb-14	11:44	127	136	120
--	--	24-Feb-14	10:36	87	75	85
Average (Range)	<b>44 (22-61)</b>	Average (Range)		<b>87 (15 – 149)</b>		

**Table 4-2 Summary of 24-hour and 1-hour TSP Monitoring Results – AM2**

Date	24-hour TSP ( $\mu\text{g}/\text{m}^3$ )	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )				
		Date	Start Time	1 <sup>st</sup> hour measured	2 <sup>nd</sup> hour measured	3 <sup>rd</sup> hour measured
27-Jan-14	68	28-Jan-14	11:57	101	98	111
4-Feb-14	35	5-Feb-14	14:51	16	19	24
10-Feb-14	43	8-Feb-14	11:28	54	52	78
15-Feb-14	36	12-Feb-14	12:27	112	130	143
21-Feb-14	32	18-Feb-14	11:47	143	112	130
--	--	24-Feb-14	10:35	89	72	78
Average (Range)	<b>43 (32-68)</b>	Average (Range)		<b>87 (16 – 143)</b>		

**Table 4-3 Summary of 24-hour and 1-hour TSP Monitoring Results – AM3**

Date	24-hour TSP ( $\mu\text{g}/\text{m}^3$ )	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )				
		Date	Start Time	1 <sup>st</sup> hour measured	2 <sup>nd</sup> hour measured	3 <sup>rd</sup> hour measured
27-Jan-14	112	28-Jan-14	15:16	116	119	109
4-Feb-14	31	5-Feb-14	11:10	14	17	24
10-Feb-14	42	8-Feb-14	11:44	67	76	62
15-Feb-14	73	12-Feb-14	9:24	137	152	126
21-Feb-14	31	18-Feb-14	14:56	156	132	126
--	--	24-Feb-14	10:17	106	74	79
Average (Range)	<b>58 (31-112)</b>	Average (Range)		<b>94 (14 – 156)</b>		

4.03 As shown in [Tables 4-1, 4-2](#) and [4-3](#), 1-hour and 24-hour TSP results fluctuated well below the Action Level during the Reporting Period.

4.04 The meteorological information during the impact monitoring days are summarized in [Appendix J](#).

## 5 IMPACT MONITORING RESULTS – CONSTRUCTION NOISE

5.01 The noise monitoring results are presented in the following sub-sections.

### Results of Construction Noise Monitoring

5.02 In this Reporting Period, a total of **20** construction noise monitoring events were undertaken at designated locations. The results for  $L_{eq30min}$  at NM1, NM2, RNM3 and NM4 are summarized in *Tables 5-1, 5-2, 5-3 and 5-4* and graphical plots are shown in *Appendix I*.

**Table 5-1 Summarized of Construction Noise Monitoring Results at NM1**

Date	Start Time	End time	1 <sup>st</sup> Leq5	2 <sup>nd</sup> Leq5	3 <sup>rd</sup> Leq5	4 <sup>th</sup> Leq5	5 <sup>th</sup> Leq5	6 <sup>th</sup> Leq5	Leq30
28-Jan-14	11:24	11:54	52.8	50.4	59.4	55.8	49.8	52.2	54.8
6-Feb-14	14:59	15:29	52.3	61.8	60.8	59.1	54.7	55.6	58.6
12-Feb-14	13:02	13:32	49.0	48.5	56.3	41.6	49.6	42.6	50.7
18-Feb-14	10:58	11:28	43.4	43.4	43.2	40.7	42.6	46.1	43.5
24-Feb-14	10:48	11:18	56.9	55.2	45.2	45.1	48.5	46.2	52.2
<b>Limit Level in dB(A)</b>									<b>75</b>

**Table 5-2 Summarized of Construction Noise Monitoring Results at NM2**

Date	Start Time	End time	1 <sup>st</sup> Leq5	2 <sup>nd</sup> Leq5	3 <sup>rd</sup> Leq5	4 <sup>th</sup> Leq5	5 <sup>th</sup> Leq5	6 <sup>th</sup> Leq5	Leq30
28-Jan-14	10:45	11:15	59.1	58.9	58.4	59.6	60.1	61.3	59.7
6-Feb-14	14:25	14:55	64.2	58.9	60.0	59.4	62.1	64.7	62.2
12-Feb-14	14:15	14:45	49.3	50.7	51.1	55.2	55.3	56.4	53.8
18-Feb-14	13:02	13:32	59.6	62.0	56.8	57.9	59.7	60.1	59.7
24-Feb-14	14:21	14:51	64.9	55.8	59.4	58.8	60.6	56.7	60.5
<b>Limit Level in dB(A)</b>									<b>75</b>

**Table 5-3 Summarized of Construction Noise Monitoring Results at RNM3**

Date	Start Time	End time	1 <sup>st</sup> Leq5	2 <sup>nd</sup> Leq5	3 <sup>rd</sup> Leq5	4 <sup>th</sup> Leq5	5 <sup>th</sup> Leq5	6 <sup>th</sup> Leq5	Leq30	Corrected* Leq30
28-Jan-14	13:55	14:25	58.0	55.4	55.4	54.9	59.1	53.0	56.4	59.4
6-Feb-14	13:09	13:39	59.4	58.4	58.8	58.2	62.7	59.7	59.8	62.8
12-Feb-14	13:39	14:09	61.5	54.3	54.4	56.0	53.3	55.2	56.8	59.8
18-Feb-14	13:35	14:05	68.1	69.7	63.9	62.3	61.1	60.1	65.7	68.7
24-Feb-14	11:30	12:00	63.8	62.1	61.0	64.4	59.5	62.4	62.5	65.5
<b>Limit Level in dB(A)</b>									<b>75</b>	

\* A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

**Table 5-4 Summarized of Construction Noise Monitoring Results at NM4**

Date	Start Time	End time	1 <sup>st</sup> Leq5	2 <sup>nd</sup> Leq5	3 <sup>rd</sup> Leq5	4 <sup>th</sup> Leq5	5 <sup>th</sup> Leq5	6 <sup>th</sup> Leq5	Leq30
28-Jan-14	13:16	13:46	45.5	43.0	46.1	43.2	42.8	53.8	48.0
6-Feb-14	13:51	14:21	48.3	50.3	52.0	55.2	51.9	53.4	52.4
12-Feb-14	14:50	15:20	50.1	42.7	40.3	40.3	40.8	42.1	44.5
18-Feb-14	10:15	10:45	51.5	47.0	40.4	45.2	47.4	45.1	47.3
24-Feb-14	15:04	15:34	49.7	48.7	49.1	50.5	49.5	48.6	49.4
<b>Limit Level in dB(A)</b>									<b>75</b>

5.03 It was noted that no noise complaint (which is an Action Level exceedance) was received. In view of the results shown in *Tables 5-1, 5-2, 5-3 and 5-4* which were all below 75dB(A), no Action or Limit Level exceedance was triggered during this month.

## 6 IMPACT MONITORING RESULTS – WATER QUALITY

- 6.01 The construction of marine outfall works was commenced on 19 July 2011 and therefore marine water quality monitoring is required in this Reporting Period. In this Reporting Period, 12 events of water quality monitoring were carried out at the designated locations.
- 6.02 The monitoring results including in-situ measurements and laboratory testing results are presented in [Appendix H](#). The graphical plots are shown in [Appendix I](#).
- 6.03 During the Reporting Period, field measurements of both control and impact stations showed that marine water of the depth average of the salinity concentration was within 32.13 to 35.75 ppt, and pH value was within 7.85 to 8.27.
- 6.04 Monitoring results of 3 key parameters: dissolved oxygen (DO), turbidity and suspended solids (SS) in this Reporting Period, are summarized in [Tables 6-1, 6-2, 6-3 and 6-4](#). A summary of exceedances for the 3 parameters are shown in [Table 6-5](#).

**Table 6-1 Summary of Water Quality Results – Mid-ebb Tides (Dissolved Oxygen)**

Sampling date	Dissolved Oxygen conc. of Depth Ave. of Surf. and Mid Layer (mg/L)						Dissolved Oxygen conc. of Depth Ave. of Bottom Layer (mg/L)					
	W1	W2	W3	C1	C2	C3	W1	W2	W3	C1	C2	C3
28-Jan-14	8.93	8.89	8.86	8.93	8.97	8.90	NA	8.86	8.86	8.75	8.93	8.84
30-Jan-14	8.66	8.69	8.85	8.86	8.65	8.78	NA	8.72	8.66	8.68	8.65	8.60
4-Feb-14	7.68	7.84	8.16	8.60	8.29	8.97	NA	7.66	7.53	7.62	8.03	7.96
6-Feb-14	7.74	8.56	8.65	8.22	8.36	8.59	NA	7.43	7.07	7.83	7.67	7.89
8-Feb-14	8.71	8.96	8.76	8.90	8.85	8.74	NA	8.77	9.01	8.77	8.74	8.71
10-Feb-14	8.07	7.89	8.00	7.78	8.64	7.67	NA	8.63	7.48	7.66	8.46	8.21
12-Feb-14	7.88	7.87	8.10	8.54	8.05	8.30	NA	8.10	8.41	8.28	8.07	8.83
15-Feb-14	7.57	7.86	8.03	8.03	8.19	8.79	NA	7.63	8.18	7.85	7.62	8.49
18-Feb-14	6.63	6.59	6.49	6.55	6.43	6.70	NA	6.62	6.29	6.38	6.36	6.82
20-Feb-14	7.59	7.59	7.96	7.50	7.65	7.48	NA	7.45	7.79	7.34	7.33	7.21
22-Feb-14	10.22	10.49	10.15	10.59	10.70	10.57	NA	10.49	10.39	10.47	10.75	10.64
24-Feb-14	11.61	11.85	10.08	11.36	10.06	11.67	NA	12.06	10.26	11.34	10.30	11.66

**Table 6-2 Summary of Water Quality Results – Mid-ebb Tides (Turbidity & Suspended Solids)**

Sampling date	Turbidity Depth Ave. (NTU)						Suspended Solids Depth Ave. (mg/L)					
	W1	W2	W3	C1	C2	C3	W1	W2	W3	C1	C2	C3
28-Jan-14	1.65	1.90	2.03	1.48	2.57	2.57	3.10	3.33	3.97	3.83	4.40	3.93
30-Jan-14	1.50	1.33	1.92	1.05	2.13	2.12	2.20	3.53	2.83	2.83	3.77	3.20
4-Feb-14	2.15	2.05	2.17	2.45	2.47	2.32	2.80	3.10	3.17	3.07	3.37	3.50
6-Feb-14	2.10	2.10	2.37	2.03	2.50	2.17	3.00	2.57	3.17	2.67	2.90	2.53
8-Feb-14	1.65	0.88	1.20	1.05	1.03	1.95	2.30	2.53	2.40	2.70	3.20	4.20
10-Feb-14	1.35	1.25	1.78	0.72	1.00	1.12	1.70	2.03	2.23	2.60	3.60	3.43
12-Feb-14	1.65	1.83	1.58	0.75	1.18	1.67	5.50	3.67	3.77	3.57	4.87	3.23
15-Feb-14	0.75	1.02	0.80	1.83	1.38	0.97	5.60	3.30	3.43	2.77	2.97	2.63
18-Feb-14	1.25	1.00	1.18	1.28	1.40	1.73	4.00	4.53	3.83	4.23	3.70	3.53
20-Feb-14	1.40	1.38	1.37	1.35	1.20	1.85	3.60	3.63	4.40	3.77	4.17	4.33
22-Feb-14	1.25	0.90	1.35	0.20	1.10	0.28	2.80	3.33	4.23	2.63	3.47	3.23
24-Feb-14	0.25	1.08	0.33	0.13	0.43	0.98	2.70	3.23	4.13	2.53	2.83	2.80

**Table 6-3 Summary of Water Quality Results – Mid-flood Tides (Dissolved Oxygen)**

Sampling date	Dissolved Oxygen conc. of Depth Ave. of Surf. and Mid Layer (mg/L)						Dissolved Oxygen conc. of Depth Ave. of Bottom Layer (mg/L)					
	W1	W2	W3	C1	C2	C3	W1	W2	W3	C1	C2	C3
28-Jan-14	8.87	8.87	8.88	8.89	8.88	8.86	NA	8.75	8.71	8.76	8.58	8.84
30-Jan-14	8.71	8.96	8.76	8.90	8.85	8.74	NA	8.77	9.01	8.77	8.74	8.71
4-Feb-14	7.78	8.38	8.38	8.01	8.14	8.78	NA	7.57	7.54	7.74	7.79	8.24
6-Feb-14	8.10	8.22	8.27	7.99	8.43	8.08	NA	8.07	8.48	8.09	8.17	7.87
8-Feb-14	8.72	8.67	8.86	8.85	8.78	8.65	NA	8.71	8.68	8.66	8.60	8.65
10-Feb-14	7.57	8.00	8.01	8.38	8.78	8.14	NA	8.54	7.74	7.54	8.24	7.79
12-Feb-14	7.07	8.28	8.43	8.56	8.47	8.06	NA	8.41	8.46	7.43	8.17	8.05
15-Feb-14	7.85	8.18	8.12	8.13	8.19	7.92	NA	8.00	7.93	7.65	7.62	7.41
18-Feb-14	6.56	7.00	6.56	7.61	6.39	7.95	NA	6.29	6.36	6.47	6.05	6.50
20-Feb-14	7.29	7.53	7.67	7.74	7.61	7.47	NA	7.61	7.46	7.25	7.19	7.36
22-Feb-14	11.68	12.89	11.07	11.46	10.94	11.88	NA	12.67	10.92	11.49	10.87	12.98
24-Feb-14	9.87	10.02	10.69	11.25	11.17	11.36	NA	10.34	11.05	11.08	10.92	11.13

**Table 6-4 Summary of Water Quality Results – Mid-flood Tides (Turbidity & Suspended Solids)**

Sampling date	Turbidity Depth Ave. (NTU)						Suspended Solids Depth Ave. (mg/L)					
	W1	W2	W3	C1	C2	C3	W1	W2	W3	C1	C2	C3
28-Jan-14	1.50	1.88	1.95	2.03	2.02	2.37	3.80	3.87	5.17	3.23	3.20	3.57
30-Jan-14	1.80	1.62	1.73	1.58	2.48	2.43	3.60	3.07	3.07	3.53	3.97	3.17
4-Feb-14	2.15	2.33	2.58	1.43	2.22	2.30	2.10	3.20	2.80	3.13	3.47	3.10
6-Feb-14	2.40	1.97	1.50	2.27	2.42	2.48	2.80	2.90	2.90	2.90	2.73	3.20
8-Feb-14	2.25	1.00	2.10	1.30	1.58	1.43	4.80	2.23	3.23	3.87	2.83	2.43
10-Feb-14	1.10	2.27	1.80	1.43	1.32	0.97	2.00	3.77	2.50	2.90	3.83	4.10
12-Feb-14	1.90	1.52	1.52	1.45	1.10	1.35	2.90	3.40	3.47	4.93	4.30	5.53
15-Feb-14	0.85	1.25	1.15	1.25	1.18	1.63	2.70	2.73	3.97	2.33	3.33	4.00
18-Feb-14	0.70	1.03	1.40	0.83	0.82	1.67	4.90	4.50	4.27	3.60	4.67	4.63
20-Feb-14	1.50	1.63	1.50	1.25	1.27	1.38	4.20	3.77	4.23	3.80	4.00	5.77
22-Feb-14	0.75	1.18	2.23	0.43	1.23	0.40	2.50	2.83	3.27	2.70	3.10	2.17
24-Feb-14	1.15	1.15	0.93	0.18	0.40	0.15	4.50	3.47	4.13	3.07	2.97	3.37

**Table 6-5 Summarized Exceedances of Marine Water Quality**

Station	DO (Ave of Surf. & mid-depth)		DO (Ave. of Bottom Layer)		Turbidity (Depth Ave.)		SS (Depth Ave)		Total Exceedance	
	Action	Limit	Action	Limit	Action	Limit	Action	Limit	Action	Limit
<b>Mid-Ebb</b>										
W1	0	0	0	0	0	0	0	0	0	0
W2	0	0	0	0	0	0	0	0	0	0
W3	0	0	0	0	0	0	0	0	0	0
<b>Mid-Flood</b>										
W1	0	0	0	0	0	0	0	0	0	0
W2	0	0	0	0	0	0	0	0	0	0
W3	0	0	0	0	0	0	0	0	0	0
No of Exceedance	0	0	0	0	0	0	0	0	0	0

6.05 For marine water monitoring, no exceedance of Action/Limit levels was recorded in this Reporting Period. Therefore, no associated corrective actions were then required.

## 7 ECOLOGY

- 7.01 According to Clause 3.7 and Figure 4 in the Environmental Permit No. EP-281/2007/A, a total of 12 numbers *Celtis Timorensis* (uncommon species) in Chung Mei at Sok Kwu Wan, are identified to require labeling, fencing and protection. Out of these, four numbers located in the Pumping Station No.1 area are required to be transplanted in advance of pumping station construction and the transplantation proposal has been submitted to EPD previously.
- 7.02 Regular inspection of the transplanted tree was carried out by the landscaping sub-Contractor (Melofield Nursery and Landscape Contractor Limited) on **30 January** and **15 February 2014**. As a contingency measure in case that CT7 to CT10 can no longer be recovered, additional 7 no. of *Celtis Timorensis* (No. CT\_1A to CT7A) were planted adjacent to the under-monitoring *Celtis Timorensis* CT7 to CT10 on 30 April 2011.
- 7.03 In April 2012, CT\_1A and CT\_7A were damaged by the fell broken tree trunk due to tree decayed by white ants. Therefore, only 5 no. of additional *Celtis Timorensis*, namely CT\_2A, CT\_3A, CT4A, CT\_5A and CT\_6A were inspected since May 2012. Furthermore, during tree inspection on 30 July, CT4A was disappeared after typhoon No.10 on 24 July 2012 and it was certified as dead. Eventually, 4 no. of additional *Celtis Timorensis*, namely CT\_2A, CT\_3A, CT\_5A and CT\_6A were inspected in the remaining period.
- 7.04 During the tree inspection on 15 August 2013, CT2A and CT3A were lost due to typhoon on 14 August 2013. Compensatory of additional *Celtis Timorensis* is recommended to carry out by the Landscape Contractor.
- 7.05 The tree inspection report for this Reporting Period is presented in [Appendix N](#).

## 8 WASTE MANAGEMENT

8.01 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

### Records of Waste Quantities

8.02 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil

8.03 The quantities of waste for disposal in this Reporting Period are summarized in [Table 8-1](#) and [8-2](#) and the Monthly Summary Waste Flow Table is shown in [Appendix K](#). Whenever possible, materials were reused on-site as far as practicable.

**Table 8-1 Summary of Quantities of Inert C&D Materials**

Type of Waste	Quantity	Disposal Location
C&D Materials (Inert) ('000m <sup>3</sup> )	0	-
Reused in the Contract (Inert) ('000m <sup>3</sup> )	0	-
Reused in other Projects (Inert) ('000m <sup>3</sup> )	0	-
Disposal as Public Fill (Inert) ('000m <sup>3</sup> )	0	-

**Table 8-2 Summary of Quantities of C&D Wastes**

Type of Waste	Quantity	Disposal Location
Metal (kg)	0	-
Paper / Cardboard Packing (kg)	0	-
Plastic (kg)	0	-
Chemical Wastes (kg)	0	-
General Refuses (tonne)	4.300	Outlying Islands Transfer Facilities (Sok Kwu Wan)

8.04 There was no site effluent discharged but the estimated volume of surface runoff was less than 50m<sup>3</sup> in this monthly period.

## 9 SITE INSPECTION

- 9.01 According to the Environmental Monitoring and Audit Manual, the environmental site inspection should be formulated by ET Leader. Regular environmental site inspections had been carried out by the ET to confirm the environmental performance. In this Reporting Period, weekly joint site inspection by RE, the Contractor and ET was carried out on **28 January and, 6, 11, 18 and 25 February 2014**.
- 9.02 The findings/ deficiencies that observed during the weekly site inspection are listed in *Table 9-1* and the relevant checklists are attached in *Appendix L*.

**Table 9-1 Site Observations**

<b>Date</b>	<b>Findings / Deficiencies</b>	<b>Follow-Up Status</b>
28 Jan 2014	<ul style="list-style-type: none"> <li>Stockpile of dusty materials without cover was observed, the Contractor was reminded to cover it with tarpaulin sheet to prevent dust disperse into air.</li> </ul>	Stockpile of dusty material has been covered with tarpaulin sheet on 6 Feb 2014.
06 Feb 2014	<ul style="list-style-type: none"> <li>No environmental issue was observed during the site inspection</li> </ul>	NA
11 Feb 2014	<ul style="list-style-type: none"> <li>No environmental issue was observed during the site inspection</li> </ul>	NA
18 Feb 2014	<ul style="list-style-type: none"> <li>Stagnant water was observed, the Contractor was reminded to spray larvicidal oil for mosquito breeding prevention.</li> </ul>	Larvicidal oil was sprayed to stagnant water on 25 Feb 2014.
25 Feb 2014	<ul style="list-style-type: none"> <li>No environmental issue was observed during the site inspection</li> </ul>	NA

## 10 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

10.01 No environmental complaint, summons and prosecution was received in this Reporting Period. The statistical summary table of environmental complaint is presented in [Tables 10-1, 10-2](#) and [10-3](#).

**Table 10-1 Statistical Summary of Environmental Complaints**

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
27 July 2010 – 31 December 2011	1 (Nov 2011)	1 (Nov 2011)	water quality
January - December 2012	0	1 (Nov 2011)	NA
January - December 2013	0	1 (Nov 2011)	NA
January 2014	0	1 (Nov 2011)	NA
February 2014	0	1 (Nov 2011)	NA

**Table 10-2 Statistical Summary of Environmental Summons**

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Complaint Nature
27 July 2010 – 31 December 2011	0	0	NA
January - December 2012	0	0	NA
January - December 2013	0	0	NA
January 2014	0	0	NA
February 2014	0	0	NA

**Table 10-3 Statistical Summary of Environmental Prosecution**

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Complaint Nature
27 July 2010 – 31 December 2011	0	0	NA
January - December 2012	0	0	NA
January - December 2013	0	0	NA
January 2014	0	0	NA
February 2014	0	0	NA



## 11 IMPLEMENTATION STATUS OF MITIGATION MEASURES

11.01 The environmental mitigation measures that recommended in the Sok Kwu Wan Environmental Monitoring and Audit covered the issues of dust, noise, water and waste and they are summarized as following:

### Dust Mitigation Measure

11.02 Installation of 2m high solid fences around the construction site of Pumping Station P2 is recommended. Implementation of the requirements stipulated in the Air Pollution Control (Construction Dust) Regulation and the following good site practices are recommended to control dust emission from the site:

- (a) Stockpiles of imported material kept on site should be contained within hoardings, dampened and / or covered during dry and windy weather;
- (b) Material stockpiled alongside trenches should be covered with tarpaulins whenever works are close to village houses;
- (c) Water sprays should be used during the delivery and handling of cement, sands, aggregates and the like.
- (d) Any vehicle used for moving sands, aggregates and construction waste shall have properly fitting side and tail boards. Materials should not be loaded to a level higher than the side and tail boards, and should be covered by a clean tarpaulin.

### Noise Mitigation Measure

11.03 As detailed in the EIA report, concreting work of the Pumping Station P1a and sewer alignment construction activities would likely cause adverse noise impacts on some of the noise sensitive receivers. Appropriate mitigation measures have therefore been recommended. The mitigation measures recommended in the EIA report are summarised below:

- (a) Use of quiet equipment for the construction activities of the Pumping Stations and sewer alignment;
- (b) Use of temporary noise barrier around the site boundary of Pumping Station P1a;
- (c) Use of kick ripper (saw and lift) method to replace the breaker for pavement removal during sewer alignment construction;
- (d) Restriction on the number of plant during sewer alignment construction;
- (e) Use of noise screening structures in the form of acoustic shed or movable barrier wherever practicable and feasible in areas with sufficient clearance and headroom during the construction of sewer alignment;
- (f) Adoption of manual working method wherever practicable and feasible in areas where the worksites of the proposed sewer alignment are located less than 20m from the residential noise sensitive receivers and less than 30m from the temple and the public library; and
- (g) Implementation of the following good site practices:
  - Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme.
  - Mobile plant, if any, should be sited as far away from NSRs as possible.
  - Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.
  - Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.
  - Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities.

### Water Quality Mitigation Measure

11.04 No-dig method using Horizontal Directional Drilling (HDD) would be used for the installation of outfall pipe of about 480 m from shore to minimize the potential water quality impacts arising from the dredging works required for the submarine outfall construction. For the remaining outfall pipe of about 240m and the diffuser section, open trench dredging would still be required.

- 11.05 During the dredging works, the Contractor should be responsible for the design and implementation of the following mitigation measures.
- Dredging should be undertaken using closed grab dredgers with a total production rate of 55m<sup>3</sup>/hr;
  - Deployment of 2-layer silt curtains with first layer enclosing the grab and the second layer at around 50, from the dredging area while dredging works are in progress;
  - all vessels should be sized such that adequate clearance (i.e. minimum clearance of 0.6m) is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash;
  - all pipe leakages should be repaired promptly and plant shall not be operated with leaking pipes;
  - excess material should be cleaned from the decks and exposed fittings of barges before the vessel is moved;
  - adequate freeboard (i.e. minimum of 200m) should be maintained on barges to ensure that decks are not washed by wave action;
  - all barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material; and
  - loading of barges and hoppers should be controlled to prevent splashing of dredged material to the surrounding water, and barges and hoppers should not be filled to a level which would cause the overflow of materials or sediment laden water during loading or transportation; and
  - the decks of all vessels should be kept tidy and free of oil or other substances that might be accidentally or otherwise washed overboard.

#### Construction Run-off and Drainage

- 11.06 The Contractor should observe and comply with the Water Pollution Control Ordinance and the subsidiary regulations. The Contractor should follow the practices, and be responsible for the design, construction, operation and maintenance of all the mitigation measures as specified in ProPECC PN 1/94 “Construction Site Drainage”. The design of the mitigation measures should be submitted by the Contractor to the Engineer for approval. These mitigation measures should include the following practices to minimise site surface runoff and the chance of erosion, and also to retain and reduce any suspended solids prior to discharge:
- Provision of perimeter channels to intercept storm-runoff from outside the site. These should be constructed in advance of site formation works and earthworks.
  - Works programmes should be designed to minimize works areas at any one time, thus minimising exposed soil areas and reducing the potential for increased siltation and runoff.
  - Sand/silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove the sand/silt particles from run-off. These facilities should be properly and regularly maintained. These facilities shall be carefully planned to ensure that they would be installed at appropriate locations to capture all surface water generated on site.
  - Careful programming of the works to minimise soil excavation works during rainy seasons.
  - Exposed soil surface should be protected by paving or hydroseeding as soon as possible to reduce the potential of soil erosion.
  - Trench excavation should be avoided in the wet season, and if necessary, these should be excavated and backfilled in short sections.
  - Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric.

#### General Construction Activities

- 11.07 Debris and rubbish generated on-site should be collected, handled and disposed of properly to avoid entering the nearby coastal waters and stormwater drains. All fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. Open drainage channels and culverts near the works areas should be covered to block the entrance of large debris and refuse.

Wastewater Arising from Workforce

- 11.08 Portable toilets shall be provided by the Contractors, where necessary, to handle sewage from the workforce. The Contractor shall also be responsible for waste disposal and maintenance practices

**Sediment Contamination Mitigation Measure**

- 11.09 The basic requirements and procedures for dredged mud disposal are specified under the WBTC No. 34/2002. The management of the dredging, use and disposal of marine mud is monitored by the MFC, while the licensing of marine dumping is the responsibility of the Director of Environmental Protection (DEP).
- 11.10 The uncontaminated dredged sediment will be loaded onto barges and transported to the designated marine disposal site. Appropriate dredging methods have been incorporated into the recommended water quality mitigation measures including the use of closed-grab dredgers and silt curtains. Category L sediment would be suitable for disposal at a gazetted open sea disposal ground.
- 11.11 During transportation and disposal of the dredged marine sediments, the following measures should be taken to minimize potential impacts on water quality:
- Bottom opening of barges should be fitted with tight fitting seals to prevent leakage of material. Excess material should be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.
  - Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels should be equipped with automatic self-monitoring devices as specified by the DEP.

**Construction Waste Mitigation Measure**

Good Site Practices and Waste Reduction Measures

- 11.12 It is not anticipated that adverse waste management related impacts would arise, provided that good site practices are strictly followed. Recommendations for good site practices for the construction waste arising include:
- Nomination of an approved person, such as a site manager, to be responsible for the implementation of good site practices, arranging for collection and effective disposal to an appropriate facility, of all wastes generated at the site.
  - Training of site personnel in proper waste management and chemical handling procedures.
  - Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.
  - Provision of sufficient waste disposal points and regular collection for disposal.
  - Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility.
  - Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.
  - Maintain records of the quantities of wastes generated, recycled and disposed.
- 11.13 In order to monitor the disposal of C&D waste at landfills and to control fly tipping, a trip-ticket system should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. An Independent Environmental Checker should be responsible for auditing the results of the system.
- 11.14 Good management and control can prevent the generation of significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:
- segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;

- to encourage collection of aluminium cans by individual collectors, separate labelled bins should be provided to segregate this waste from other general refuse generated by the work force;
- any unused chemicals or those with remaining functional capacity should be recycled;
- use of reusable non-timber formwork to reduce the amount of C&D material;
- prior to disposal of C&D waste, it is recommended that wood, steel and other metals should be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill;
- proper storage and site practices to minimise the potential for damage or contamination of construction materials; and
- plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.

#### General Site Wastes

- 11.15 A collection area should be provided where waste can be stored prior to removal from site. An enclosed and covered area is preferred for the collection of the waste to reduce 'wind blow' of light material.

#### Chemical Wastes

- 11.16 After use, chemical waste (eg. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Any unused chemicals or those with remaining functional capacity should be recycled. Spent chemicals should be properly stored on site within suitably designed containers, and should be collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licenced facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation under the Waste Disposal Ordinance.
- 11.17 Any service shop and minor maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakages and spillage should only be undertaken with the areas appropriately equipped to control these discharges.

#### Construction and Demolition Material

- 11.18 The C&D material should be separated on-site into three categories: (i) public fill, the inert portion of the C&D material (e.g. concrete and rubble), which should be re-used on-site or disposed of at a public filling area; (ii) C&D waste for re-use and/or recycling, the non-inert portion of the C&D material, (e.g. steel and other metals, wood, glass and plastic); (iii) C&D waste which cannot be re-used and/or recycled. The waste producers are responsible for its disposal at strategic landfills.
- 11.19 In order to minimise the impact resulting from collection and transportation of material for off-site disposal, it was recommended that inert material should be re-used on-site where possible. Prior to disposal of C&D material, it was also recommended that steel and other metals should be separated for re-use and/or recycling where practicable to minimise the quantity of waste to be disposed of to landfill.

#### Ecology Mitigation Measure

##### Terrestrial Ecology

- 11.20 The uncommon tree species should be labelled and probably fenced to avoid direct or indirect disturbance during construction. Works areas should avoid woodland habitats, in particular where these trees are located.
- 11.21 Construction and maintenance of site runoff control measures would be required at all work sites during construction. These should include barriers to direct runoff to sand/silt removal facilities (sand/silt/traps and/or sediment basins); minimisation of earthworks during rainy season (May to September); and coverage of sand/fill piles and exposed earth during storms.

11.22 Special attention should be paid during the breeding season of Romer’s Tree Frog (March to September) to ensure their habitat landward to Pumping Station P2 site is well protected from site runoff. Barriers should be deployed completely along the landward side of the pumping station site boundary to prevent any site runoff from entering the tree frog habitat. Intactness of the barriers should be frequently inspected.

Intertidal and Subtidal Ecology

11.23 Construction and maintenance of site runoff control measures would be required at all work sites during construction. These should include barriers to direct runoff to sand/silt removal facilities (sand/silt/traps and/or sediment basins); use of silt curtains along coastline; minimisation of earthworks during rainy season (May to September); and coverage of sand/fill piles and exposed earth during storms.

11.24 To reduce impacts of sediment resuspension upon nearby habitats and organisms during dredging, all dredging should be done using a closed-grab dredger, and silt curtains should be deployed around the dredger during all dredging activity

Fisheries Mitigation Measure

11.25 Closed grab dredger, deployment of silt curtains around the immediate dredging area and low dredging rate have been recommended in Water Quality of the EIA report in order to minimise sediment release into the water column.

Landscape & Visual Mitigation Measure

11.26 Mitigation measures recommended in the EIA Report for landscape and visual impacts during the construction stage are summarised below.

- Screening of site construction works by use of hoarding that is appropriate to its site context;
- Retaining existing trees and minimising damage to vegetation where possible by close co-ordination and on site alignment adjusted of rising main and gravity sewer pipelines. Tree protective measures should be implemented to ensure trees identified as to be retained are satisfactorily protected during the construction phase;
- Careful and efficient transplanting of affected trees (1 no.) to temporary or final transplant location (the proposed tree to be transported is a semi-mature *Macaranga tanarius* and is located at the proposed Pumping Station P2 location);
- Short excavation and immediate backfilling of sections upon completion of works to reduce active site area;
- Conservation of top-soil for reuse.
- Night-time light source from marine fleets should be directed away from the residential units

11.27 The implementation schedule of mitigation measures is presented in [Appendix M](#).

11.28 Leader had been implementing the required environmental mitigation measures according to the Sok Kwu Wan Environmental Monitoring and Audit Manual subject to the site condition. Environmental mitigation measures generally implemented by Leader in this Reporting Period are summarized in [Table 11-1](#).

**Table 11-1 Environmental Mitigation Measures**

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> <li>• Drainage channels were provided to convey run-off into the treatment facilities; and</li> <li>• Drainage systems were regularly and adequately maintained.</li> </ul>
Air Quality	<ul style="list-style-type: none"> <li>• Cover all excavated or stockpile of dusty material by impervious sheeting or sprayed with water to maintain the entire surface wet;</li> <li>• Public roads around the site entrance/exit had been kept clean and free from dust; and</li> <li>• Tarpaulin covering of any dusty materials on a vehicle leaving the site.</li> </ul>

Issues	Environmental Mitigation Measures
Noise	<ul style="list-style-type: none"><li>• Good site practices to limit noise emissions at the sources;</li><li>• Use of quiet plant and working methods;</li><li>• Use of site hoarding or other mass materials as noise barrier to screen noise at ground level of NSRs; and</li><li>• To minimize plant number use at the worksite.</li></ul>
Waste and Chemical Management	<ul style="list-style-type: none"><li>• Excavated material should be reused on site as far as possible to minimize off-site disposal. Scrap metals or abandoned equipment should be recycled if possible;</li><li>• Waste arising should be kept to a minimum and be handled, transported and disposed of in a suitable manner;</li><li>• The Contractor should adopt a trip ticket system for the disposal of C&amp;D materials to any designed public filling facility and/or landfill; and</li><li>• Chemical waste shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes.</li></ul>
General	<ul style="list-style-type: none"><li>• The site was generally kept tidy and clean.</li></ul>

## 12 IMPACT FORECAST

12.01 Key issues to be considered in the coming month include:

### Water Quality

- Erect of sand bag in proper area to avoid any muddy surface runoff from the loose soil surface or haul road during the rainy days; and
- The accumulated stagnant water should be drained away.

### Air Quality

- Vehicles shall be cleaned of mud and debris before leaving the site;
- Stockpile and loose soil surface shall be covered with tarpaulin sheet or other means to eliminate the fugitive dust;
- Water spaying on the dry haul road and exit/entrance of the site in regular basis is reminded; and
- Public roads around the site entrance/exit had been kept clean and free from dust.

### Noise

- Works and equipment should be located to minimize noise nuisance from the nearest sensitive receiver; and
- Idle equipments should be either turned off or throttled down;

### Waste and Chemical Management

- Housekeeping on site shall be improved;
- The Contractor is advised to fence off the construction waste at a designated area in order to maintain the tidiness of the site;
- Drip tray and proper label should be provided for all chemical containers.
- C&D waste should be disposed in regular basis.

### 13 CONCLUSIONS AND RECOMMENDATIONS

#### CONCLUSIONS

- 13.01 This is the **43<sup>rd</sup>** monthly EM&A Report covering the construction period from **26 January to 25 February 2014**.
- 13.02 In this Reporting Period, no 1-hour and 24-hour TSP results were found to be triggered the Action or Limit Level
- 13.03 No noise complaint (an Action Level exceedance) was received and no construction noise measurement results that exceeded the Limit Level were recorded in this Reporting Period.
- 13.04 The monitoring result demonstrated no exceedance of Action or Limit Level of marine water quality monitoring in this Reporting Period.
- 13.05 No documented complaint, notification of summons or successful prosecution was received.
- 13.06 In this Reporting Period, weekly joint site inspection by RE, the Contractor and ET was carried out on **28 January and, 6, 11, 18 and 25 February 2014**. All the observation has been rectified in the set time frame. The environmental performance of the Project was therefore considered as satisfactory.


#### RECOMMENDATIONS

- 13.07 During dry and windy season, the Contractor shall pay attention on the construction dust that may cause environmental issues in the upcoming months. Mitigation measures on construction dust identified at the EM&A manual such as watering at haul road and covering of dusty material should be fully implemented.
- 13.08 Muddy water and other water quality pollutants via site surface water runoff into the sea body within Fish Culture Zone (FCZ) at Picnic Bay and the secondary recreation contact subzone at Mo Tat Wan is the key issue of the Project. Mitigation measures for water quality should be properly maintained to prevent any muddy or sandy runoff from the loose soil surface overflow on the site boundary.



## **Appendix A**

### **Site Layout Plan – Sok Kwu Wan Portion Area**

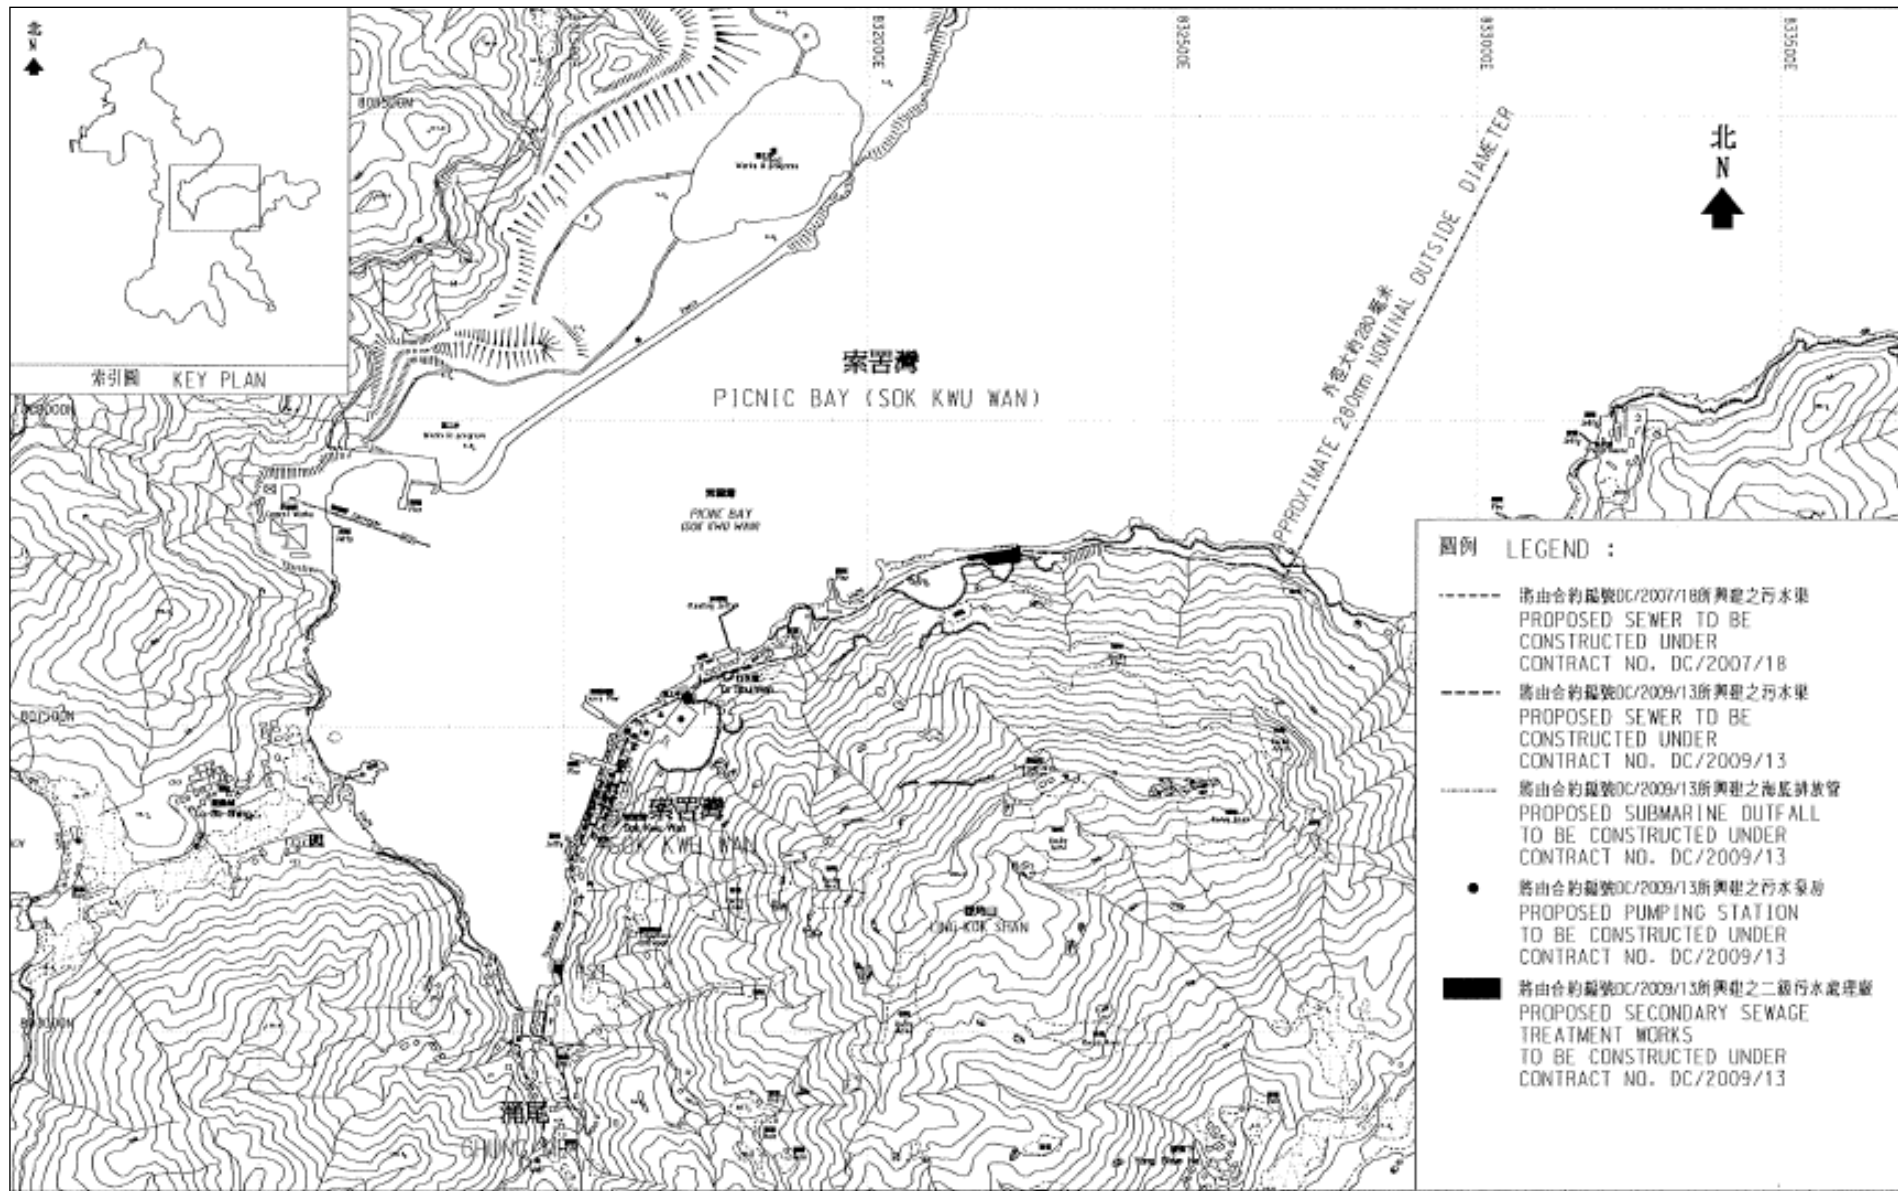

## **Appendix B**

### **Organization Structure and Contact Details of Relevant Parties**

Contact Details of Key Personnel

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
DSD	Employer	Ms. Jacky C.M. Wong	2159-3413	2833-9162
SCJV	Engineer's Representative	Mr. Ian Jones	2982 0240	2982 4129
URS	Independent Environmental Checker	Mr. Rodney Ip	2410 3750	2428 9922
Leader	Director	Mr. Wilfred So	2982 1750	2982 1163
Leader	Project Manager	Mr. Vincent Chan	2982 1750	2982 1163
Leader	Construction Manager	Mr. Ron Hung	2982 1750	2982 1163
Leader	Environmental Officer	Mr. Leung Man Kin	2982 8652	2982 8650
Leader	Environmental Supervisor	Mr. Chan Chi Kau	2982 8652	2982 8650
Leader	Sub-Agent	Mr. Leung Man Kin	2982 1750	2982 1163
Leader	Senior Safety Officer	Mr. Andy Lau	2982 1750	2982 1163
AUES	Environmental Team Leader	Mr. T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959 6059	2959 6079
AUES	Team Supervisor	Mr. Ben Tam	2959 6059	2959 6079

Legend:

*DSD (Employer) – Drainage Services Department*

*CDM (Engineer) –URS Hong Kong Limited CDM Joint Venture*

*Leader (Main Contractor) – Leader Civil Engineering Corporation Limited*

*URS (IEC) – URS Hong Kong Limited*

*AUES (ET) – Action-United Environmental Services & Consulting*

## **Appendix C**

### **Three Months Rolling Construction Programme**









Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	OCT	2013 NOV	DEC	JAN	2014 FEB	MAR	
<b>YSW STW - GL T - X</b>																	
YSW0610	Excavate to formation	10	100	08/09/10 A	17/09/10 A	08/09/10 A	17/09/10 A		YSW0035, YSW0422	YSW0620							
YSW0620	Base slab construction	248	100	18/09/10 A	23/05/11 A	18/09/10 A	23/05/11 A		YSW0610	YSW0630							
YSW0630	G/F to 1/F construction	205	100	24/05/11 A	14/12/11 A	24/05/11 A	14/12/11 A		YSW0620	YSW0640							
YSW0640	1/F to Roof Construction	64	100	15/12/11 A	16/02/12 A	15/12/11 A	16/02/12 A		YSW0630	YSW0810							
YSW0810	ABWF installation	80	100	28/12/11 A	16/03/12 A	28/12/11 A	16/03/12 A		YSW0640	E&M0610, E&M0620, E&M0630,							
<b>YSW STW - GL F - H &amp; DN Tanks</b>																	
YSW0650	ELS & Excavation for DN Tanks	37	100	08/09/10 A	14/10/10 A	08/09/10 A	14/10/10 A		YSW0035, YSW0422	YSW0660							
YSW0660	Sub-structure construction (DN Tanks)	78	100	15/10/10 A	31/12/10 A	15/10/10 A	31/12/10 A		YSW0650	YSW0530, YSW0670							
YSW0670	Backfill & Remove ELS (DN Tanks)	70	100	01/01/11 A	11/03/11 A	01/01/11 A	11/03/11 A		YSW0660	YSW0680							
YSW0680	Base slab construction (SD1, SD2 & MBR4)	17	100	12/03/11 A	28/03/11 A	12/03/11 A	28/03/11 A		YSW0670	YSW0690							
YSW0690	Construct Superstructure SD1, SD2 & MBR4	82	100	29/03/11 A	18/06/11 A	29/03/11 A	18/06/11 A		YSW0680	YSW0710, YSW0820							
YSW06901	Construct Superstructure of DN Tanks	28	100	15/05/12 A	11/06/12 A	15/05/12 A	11/06/12 A		YSW0735	YSW0830							
YSW0705	Water test for MBR 4	47	100	01/10/12 A	16/11/12 A	01/10/12 A	16/11/12 A		YSW0710	E&M0510, E&M0640, YSW07055,							
YSW07055	Water test for SD1 & SD2	54	100	17/11/12 A	10/01/13 A	17/11/12 A	10/01/13 A		YSW0705, YSW07105	E&M0610							
YSW0710	Apply protective paint for MBR 4	7	100	24/09/12 A	30/09/12 A	24/09/12 A	30/09/12 A		YSW0690	YSW0705, YSW07105							
YSW07105	Apply protective paint for SD1 & SD2	7	100	01/10/12 A	07/10/12 A	01/10/12 A	07/10/12 A		YSW0710	YSW07055							
YSW0830	Water test for DN Tanks	28	100	14/07/13 A	13/09/13 A	14/07/13 A	13/09/13 A		YSW06901	YSW0850	Water test for DN Tanks						
YSW0850	Apply protective paint for DN Tanks	6	100	27/04/13 A	11/07/13 A	27/04/13 A	11/07/13 A		YSW0830	E&M0610							
<b>YSW STW - GL A - F</b>																	
YSW0730	Completion of HDD	0	100	21/01/12 A		21/01/12 A			YSW03601, YSW03605	YSW0732							
YSW0732	Excavate for MBR 2 & 3	20	100	21/01/12 A	09/02/12 A	21/01/12 A	09/02/12 A		YSW0730	YSW0733							
YSW0733	Construct basement of MBR 2 & 3	20	100	10/02/12 A	29/02/12 A	10/02/12 A	29/02/12 A		YSW0732	YSW0735, YSW0740							
YSW0735	Construct superstructure of MBR 2	75	100	01/03/12 A	14/05/12 A	01/03/12 A	14/05/12 A		YSW0733	YSW06901, YSW0736, YSW08302,							
YSW0736	Construct superstructure of MBR 3	100	100	15/05/12 A	14/05/12 A	15/05/12 A	14/05/12 A		YSW0735	YSW08302, YSW08305							
YSW0740	ELS & excavate for Outfall Shaft	75	100	01/03/12 A	14/05/12 A	01/03/12 A	14/05/12 A		YSW0733	YSW0750							
YSW0750	Construct basement of Outfall Shaft	19	100	15/05/12 A	02/06/12 A	15/05/12 A	02/06/12 A		YSW0740	YSW07501							
YSW07501	Connect additional flange to HDPE pipe (VO 042)	5	100	03/06/12 A	07/06/12 A	03/06/12 A	07/06/12 A		YSW0750	YSW07502							
YSW07502	Construct sub-structure of Outfall Shaft	16	100	08/06/12 A	23/06/12 A	08/06/12 A	23/06/12 A		YSW07501	YSW0760							
YSW0760	Backfill & remove ELS (outfall shaft)	8	100	24/06/12 A	01/07/12 A	24/06/12 A	01/07/12 A		YSW07502	YSW01800, YSW07601, YSW07603,							
YSW07601	Construct superstructure for Outfall Shaft	30	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		YSW0760	YSW08301, YSW08305							
YSW07603	ELS & excavate for FSH Water Supply Tank	25	100	01/06/12 A	25/06/12 A	01/06/12 A	25/06/12 A		YSW0760	YSW07604							
YSW07604	Construct substructure for FSH Water Supply Tank	24	100	26/06/12 A	19/07/12 A	26/06/12 A	19/07/12 A		YSW07603	YSW07605							
YSW07605	Backfill & remove ELS for FSH Water Supply Tank	12	100	20/07/12 A	31/07/12 A	20/07/12 A	31/07/12 A		YSW07604	YSW07607							
YSW07607	Construct basement of MBR 1 & Workshop	24	100	01/08/12 A	24/08/12 A	01/08/12 A	24/08/12 A		YSW07605	YSW07608, YSW07609							
YSW07608	Construct superstructure for FSH Water Supply Tk	37	100	25/08/12 A	30/09/12 A	25/08/12 A	30/09/12 A		YSW07607	YSW08304, YSW08305							
YSW07609	Construct superstructure for MBR 1	37	100	25/08/12 A	30/09/12 A	25/08/12 A	30/09/12 A		YSW07607	YSW07610, YSW08303, YSW1470							
YSW07610	Construct Workshop, FSSH Pump Rm, PW Pump Rm	31	100	03/10/12 A	31/10/12 A	03/10/12 A	31/10/12 A		YSW07609	YSW0840, YSW16606, YSW16607,							
YSW08301	Water tightness test for Outfall Shaft	42	100	03/04/13 A	18/04/13 A	03/04/13 A	18/04/13 A		YSW0380, YSW07601	E&M0690							
YSW08302	Water tightness test for MBR 2 & 3	95	100	10/08/13 A	24/08/13 A	10/08/13 A	24/08/13 A		YSW0735, YSW0736	E&M0520, E&M0590, E&M0605,	Water tightness test for MBR 2 & 3						
YSW08303	Water tightness test for MBR 1	19	100	30/11/12 A	18/12/12 A	30/11/12 A	18/12/12 A		YSW07609	E&M0520							
YSW08304	Water tightness test for FSH Water Supply Tank	32	100	31/08/13 A	01/10/13 A	31/08/13 A	01/10/13 A		YSW07608	E&M0610	Water tightness test for FSH Water Supply Tank						
<b>Fire Hose Reel / Sprinkler Pump Rm</b>																	
YSW08305	Apply protective paint	120	100	02/10/12 A	15/08/13 A	02/10/12 A	15/08/13 A		YSW0735, YSW0736, YSW07601,	E&M0610							
YSW0840	ELS & excavate to formation (+0 mPD approx.)	40	100	25/02/13 A	18/04/13 A	25/02/13 A	18/04/13 A		YSW07610, YSW16606	YSW0860							
YSW0860	Sub-structure construction	40	100	19/04/13 A	12/06/13 A	19/04/13 A	12/06/13 A		YSW0840	YSW0890							
YSW0880	Backfill & remove ELS	35	100	21/06/13 A	26/08/13 A	21/06/13 A	26/08/13 A		YSW0890	YSW0910	ELS						
YSW0890	Construction Ground Slab at +5.2mPD	40	100	04/06/13 A	14/07/13 A	04/06/13 A	14/07/13 A		YSW0860	YSW0880, YSW0900							
YSW0900	Superstructure construction upto +9.2mPD	35	100	04/06/13 A	01/08/13 A	04/06/13 A	01/08/13 A		YSW0890	YSW0910, YSW0925	+9.2mPD						
YSW0910	Water test	28	0	30/11/13	27/12/13	30/10/13	27/11/13	-30d	YSW0880, YSW0900	YSW0915							
YSW0915	Apply protective paint	14	0	28/12/13	10/01/14	27/11/13	11/12/13	-30d	YSW0910	E&M0640, YSW0925							
YSW0925	ABWF installation	30	35	16/07/13 A	10/01/14	16/07/13 A	16/06/14	157d	YSW0900, YSW0915	KD0040							
<b>Emergency Storage Tank</b>																	
YSW1470	ELS & excavate to formation (-1.5mPD Approx.)	16	100	17/09/12 A	02/10/12 A	17/09/12 A	02/10/12 A		YSW07609	YSW1480							
YSW1480	Sub-structure construction	14	100	03/10/12 A	16/10/12 A	03/10/12 A	16/10/12 A		YSW1470	YSW1490							

Start date 05/05/10  
Finish date 20/10/17  
Data date 30/11/13  
Run date 04/03/14  
Page number 4A  
© Primavera Systems, Inc.

- █ Early bar
- █ Progress bar
- █ Critical bar
- █ Summary bar
- ▲ Progress point
- ▼ Critical point
- ◆ Summary point
- ◆ Start milestone point
- ◆ Finish milestone point

Leader Civil Engineering Corp. Ltd.  
Contract No. DC/2009/13  
Construction of Sewage Treatment Works at YSW & SKW  
3-month Rolling Programme (Feb 2014 - April 201)

Date	Revision	Checked	Approved
31/01/14	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	OCT	2013 NOV	DEC	JAN	2014 FEB	MAR
YSW1490	Backfill & extract sheetpile	3	100	17/10/12 A	19/10/12 A	17/10/12 A	19/10/12 A		YSW1480	YSW1500						
YSW1500	Superstructure construction upto +10.5mPD	41	100	20/10/12 A	29/11/12 A	20/10/12 A	29/11/12 A		YSW1490	YSW1530, YSW1536						
YSW1530	Underground pipeline works	40	100	20/07/13 A	01/10/13 A	20/07/13 A	01/10/13 A		YSW1500	E&M0690, YSW1680	Underground pipeline works					
YSW1538	Apply protective paint	30	100	04/03/13 A	05/03/13 A	04/03/13 A	05/03/13 A		YSW1536	YSW1540						
YSW1540	ABWF installation	40	100	03/04/13 A	01/10/13 A	03/04/13 A	01/10/13 A		YSW1538	E&M0690	ABWF installation					
<b>Road, Drain, Cable Draw Pits &amp; Ducting</b>																
YSW16601	ELS & excavate 6m deep sewer (FM1 - YFMH13)	90	100	04/08/13 A	15/01/14 A	04/08/13 A	15/01/14 A		YSW0760, YSW16606, YSW16607,	YSW16602	ELS & excavate 6m deep sewer (FM1 -					
YSW16602	Lay pipe & backfill 6m deep sewer (FM1 - YFMH13)	45	100	20/01/14 A	10/02/14 A	20/01/14 A	10/02/14 A		YSW16601	E&M0680, YSW1700	Lay pipe & backfill 6m dee					
YSW16603	Construct UU & pipes along sea side (Grid Q-X)	60	0	04/03/14 A	28/01/14	04/03/14 A	16/11/13	-73d	YSW16607, YSW16608	YSW16604, YSW16703	Construct UU & pipes along sea					
YSW16604	Construct UU & pipes along sea side (Grid XA-D)	60	100	22/07/13 A	06/02/14 A	22/07/13 A	06/02/14 A		YSW16603	YSW16605, YSW16701	Construct UU & pipes along					
YSW16606	Construct UU & pipes along hill side (Grid D-Q)	90	100	10/10/12 A	01/09/13 A	10/10/12 A	01/09/13 A		YSW07610	YSW0840, YSW16601	pipes along hill side (Grid D-Q)					
YSW16607	Construct UU & pipes along hill side ( Grid Q-X)	72	100	20/08/12 A	01/09/13 A	20/08/12 A	01/09/13 A		YSW07610	YSW16601, YSW16603	pipes along hill side ( Grid Q-X)					
YSW16608	Construct UU & pipes along hill side (Grid XA-D)	72	100	30/11/12 A	01/09/13 A	30/11/12 A	01/09/13 A		YSW07610	YSW16601, YSW16603, YSW1690	pipes along hill side (Grid XA-D)					
YSW16701	Construct Boundary Wall (Grid XA-D)	80	100	10/01/13 A	15/12/13 A	10/01/13 A	15/12/13 A		YSW16604	YSW16702	Construct Boundary Wall (Grid XA-D)					
YSW16702	Construct Boundary Wall (Grid D-Q)	80	50	01/01/14 A	21/03/14	01/01/14 A	07/01/14	-73d	YSW16605, YSW16701	YSW16703	Cons					
YSW16703	Construct Boundary Wall (Grid Q-X)	80	0	22/03/14	09/06/14	08/01/14	28/03/14	-73d	YSW16603, YSW16702	YSW16704, YSW1700						
YSW16704	ABWF installation for Boundary Wall	240	0	01/01/14	28/08/14	20/10/13	16/06/14	-73d	YSW16703	KD0040						
YSW1680	Fire Hydrant & pipeline installation	120	60	26/01/13 A	16/01/14	26/01/13 A	20/02/14	35d	YSW1530	YSW1690, YSW1700	Fire Hydrant & pipeline installation					
YSW1690	Construction of Road Kerbs, Downpipes, U-channel	180	60	02/01/13 A	29/03/14	02/01/13 A	03/05/14	35d	YSW16608, YSW1680	YSW1700						
YSW1700	Road Paving	110	60	23/05/14 A	23/07/14	23/05/14 A	16/06/14	-37d	YSW16602, YSW16605, YSW16703, YSW1680, YSW1690	KD0040						
<b>Submarine Outfall</b>																
YSW0180	Coordination of HEC	53	100	17/05/10 A	08/07/10 A	17/05/10 A	08/07/10 A		KD0020	YSW0350						
YSW0200	Submission and Approval of Ecologist	60	100	17/05/10 A	15/07/10 A	17/05/10 A	15/07/10 A		KD0020	YSW0210						
YSW0210	Ecology Survey	211	100	16/07/10 A	11/02/11 A	16/07/10 A	11/02/11 A		YSW0200	YSW0350						
YSW0220	Submission and Approval of In. Hydro Survey	103	100	17/05/10 A	27/08/10 A	17/05/10 A	27/08/10 A		KD0020	YSW0230						
YSW0230	Hydrographical Survey (YSW)	157	100	28/08/10 A	31/01/11 A	28/08/10 A	31/01/11 A		YSW0220	YSW0350						
YSW0240	Material Submission, Approval of HDPE pipe	319	100	17/05/10 A	31/03/11 A	17/05/10 A	31/03/11 A		KD0020	YSW0360						
YSW02401	Clarify Coordinate of Point Y (Reply of RFI 010)	83	100	28/06/10 A	18/09/10 A	28/06/10 A	18/09/10 A		KD0020	YSW0250						
YSW0250	Submit and Approval of Method Statement for HDD	188	100	19/09/10 A	25/03/11 A	19/09/10 A	25/03/11 A		YSW02401	YSW0260, YSW0270, YSW0340						
YSW0260	Submission of HDD Method Statement to HEC	14	100	26/03/11 A	08/04/11 A	26/03/11 A	08/04/11 A		YSW0250	YSW0340						
YSW0270	Additional G.I. Boreholes (YSW)	123	100	19/09/10 A	19/01/11 A	19/09/10 A	19/01/11 A		YSW0250	YSW0280, YSW0290						
YSW0280	Submission of propose alignment	44	100	20/01/11 A	04/03/11 A	20/01/11 A	04/03/11 A		YSW0270	YSW0310, YSW0340						
YSW0290	Submission of Marine Notice	69	100	20/01/11 A	29/03/11 A	20/01/11 A	29/03/11 A		YSW0270	YSW0350						
YSW0310	Construction of Entry Pit and Preparation Work	27	100	05/03/11 A	31/03/11 A	05/03/11 A	31/03/11 A		YSW0280	YSW0320						
YSW0320	Prepare of HDD Drill Rig Set-up (YSW)	28	100	01/04/11 A	28/04/11 A	01/04/11 A	28/04/11 A		YSW0310	YSW0330, YSW0350						
YSW0330	Establishment of HDD plant & equipment	6	100	09/04/11 A	14/04/11 A	09/04/11 A	14/04/11 A		YSW0320	YSW0340						
YSW0340	Setting up at drillhole location	14	100	15/04/11 A	28/04/11 A	15/04/11 A	28/04/11 A		YSW0250, YSW0260, YSW0280,	YSW0350						
YSW0350	Drill pilot hole and reaming hole - NS400 - 530m	229	100	29/04/11 A	13/12/11 A	29/04/11 A	13/12/11 A		YSW0040, YSW0180, YSW0210,	YSW0360						
YSW0360	Installation of NS400 HDPE 530m	17	100	14/12/11 A	30/12/11 A	14/12/11 A	30/12/11 A		YSW0240, YSW0350	SKW1181, YSW03601, YSW03620,						
YSW03601	Demobilization of HDD plant & equipment	7	100	31/12/11 A	06/01/12 A	31/12/11 A	06/01/12 A		YSW0360	YSW03605, YSW03641, YSW0730						
YSW03605	Remove Entry pit of HDD	14	100	07/01/12 A	20/01/12 A	07/01/12 A	20/01/12 A		YSW03601	YSW0730						
YSW03620	Removal of Receiving Pit	14	100	31/12/11 A	13/01/12 A	31/12/11 A	13/01/12 A		YSW0360	YSW0365						
YSW03641	Prepare backfilling material under VO 046A	120	100	07/01/12 A	05/05/12 A	07/01/12 A	05/05/12 A		YSW03601	YSW0365						
YSW0365	Set up of Silt Curtain as per EP	2	100	23/11/12 A	24/11/12 A	23/11/12 A	24/11/12 A		SKW1431, YSW03620, YSW03641	YSW0370						
YSW0370	Dredging of Marine Deposit for Diffuser (YSW)	5	100	24/11/12 A	29/11/12 A	24/11/12 A	29/11/12 A		YSW0360, YSW0365	YSW0380						
YSW0380	Diffuser Construction (YSW)	60	100	30/11/12 A	20/06/13 A	30/11/12 A	20/06/13 A		YSW0370	E&M0690, YSW0400, YSW08301						
YSW0400	Removal of silt curtain	30	100	30/04/13 A	31/05/13 A	30/04/13 A	31/05/13 A		YSW0380	KD0040						
<b>E&amp;M Works - YSW STW</b>																
E&M0360	Delivery of MBR Memb. Mod. (MBR Tk 4)	118	100	24/02/11 A	21/06/11 A	24/02/11 A	21/06/11 A		E&M0160	E&M0510						
E&M0370	Delivery of MBR Membrane Modules - 2nd Shipment	236	100	24/02/11 A	17/10/11 A	24/02/11 A	17/10/11 A		E&M0160	E&M0520						
E&M0380	Delivery of Grit Removal Equipment	81	100	10/10/11 A	29/12/11 A	10/10/11 A	29/12/11 A		E&M0150	E&M0530						
E&M0390	Delivery of Coarse Screens	129	100	06/09/11 A	12/01/12 A	06/09/11 A	12/01/12 A		E&M0110	E&M0540						
E&M0400	Delivery of Fine Screens	80	100	12/09/11 A	30/11/11 A	12/09/11 A	30/11/11 A		E&M0120	E&M0550						
E&M0410	Delivery of Pumps	75	100	23/06/11 A	05/09/11 A	23/06/11 A	05/09/11 A		E&M0130	E&M0560						
E&M0420	Delivery of Submersible Mixers	230	100	26/02/11 A	26/02/11 A	26/02/11 A	26/02/11 A		E&M0140	E&M0570						

Start date	05/05/10
Finish date	20/10/17
Data date	30/11/13
Run date	04/03/14
Page number	5A
c Primavera Systems, Inc.	

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ▲ Progress point
- ▼ Critical point
- ◆ Summary point
- ◆ Start milestone point
- ◆ Finish milestone point

**Leader Civil Engineering Corp. Ltd.**  
**Contract No. DC/2009/13**  
**Construction of Sewage Treatment Works at YSW & SKW**  
**3-month Rolling Programme (Feb 2014 - April 201)**

Date	Revision	Checked	Approved
31/01/14	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013					2014		
											OCT	NOV	DEC	JAN	FEB	MAR		
E&M0440	Delivery of Sludge Dewatering Equipment	558	70	31/08/11 A	16/05/14	31/08/11 A	30/10/13	-198d	E&M0170	E&M0580								
E&M0450	Delivery of Valves, Pipes & Fittings	560	90	30/08/11 A	26/02/14	30/08/11 A	01/01/14	-56d	E&M0180	E&M0590								
E&M0460	Delivery of Penstocks	135	100	12/08/11 A	24/12/11 A	12/08/11 A	24/12/11 A		E&M0190	E&M0600, E&M0605								
E&M0470	Delivery of Instruments	232	100	03/11/11 A	21/06/11 A	03/11/11 A	21/06/11 A		E&M0200	E&M0610								
E&M0480	Delivery of MCC LVSB	90	100	03/12/12 A	04/03/13 A	03/12/12 A	04/03/13 A		E&M0210	E&M0620								
E&M0490	Delivery of BS Equipment	446	65	10/12/11 A	17/02/15	10/12/11 A	23/06/13	-604d	E&M0220	E&M0630								
E&M0500	Delivery FS Equipment	507	25	11/12/11 A	11/10/15	11/12/11 A	14/08/13	-788d	E&M0230	E&M0330, E&M0640								
E&M0510	Install Membrane Modules in MBR Tank no. 4	89	100	03/11/12 A	28/02/13 A	03/11/12 A	28/02/13 A		E&M0360, YSW0705	E&M0690								
E&M0520	Install Membrane Modules in MBR Tank No. 1 to 3	57	100	03/12/12 A	28/02/13 A	03/12/12 A	28/02/13 A		E&M0370, YSW08302, YSW08303	E&M0690								
E&M0530	Install Grit Removal Equipment	122	100	01/06/12 A	30/09/12 A	01/06/12 A	30/09/12 A		E&M0380, YSW05923	E&M0590, E&M0660								
E&M0540	Install Coarse Screens	240	100	23/04/12 A	23/08/13 A	23/04/12 A	23/08/13 A		E&M0390, YSW05923	E&M0660								
E&M0550	Install Fine Screens	122	100	01/06/12 A	12/08/13 A	01/06/12 A	12/08/13 A		E&M0400, YSW05923	E&M0590, E&M0660								
E&M0560	Install Pumps	355	90	23/04/12 A	04/01/14	23/04/12 A	12/05/13	-237d	E&M0410, YSW05923	E&M0660								
E&M0570	Install Submersible Mixers	163	90	15/01/13 A	16/12/13	15/01/13 A	12/05/13	-218d	E&M0420, YSW07204	E&M0660, E&M0690								
E&M0580	Install Sludge Dewatering Equipment	361	60	29/05/12 A	23/04/14	29/05/12 A	09/06/13	-318d	E&M0440, YSW06023	E&M0690								
E&M0590	Install Valves, Pipes & Fittings	232	85	15/01/13 A	03/01/14	15/01/13 A	10/06/13	-207d	E&M0450, E&M0530, E&M0550, E&M0460, YSW07202	E&M0650, E&M0690								
E&M0600	Install Penstocks (Batch 1, GL H - T)	213	100	23/04/12 A	21/05/13 A	23/04/12 A	21/05/13 A		E&M0460, YSW07202	E&M0690								
E&M0605	Install Penstocks (Batch 2, GL A - F)	131	85	02/01/13 A	19/12/13	02/01/13 A	08/06/13	-194d	E&M0460, YSW08302	E&M0690								
E&M0610	Install Instruments	74	5	02/01/13 A	08/02/14	02/01/13 A	10/06/13	-243d	E&M0470, YSW07055, YSW0810, E&M0480, YSW0810	E&M0660, E&M0680								
E&M0620	Install SAT, MCC & LVSB	8	100	02/01/13 A	02/01/15 A	02/01/13 A	02/01/15 A		E&M0490, YSW0810, YSW0820	E&M0690								
E&M0630	Install BS Equipment	180	55	02/01/13 A	10/03/15	02/01/13 A	14/07/13	-604d	E&M0500, YSW0705, YSW0810, E&M0590, YSW08302	E&M0690								
E&M0640	Install FS Equipment	180	50	02/01/13 A	10/09/15	02/01/13 A	14/07/13	-788d	E&M0530, E&M0540, E&M0550, E&M0560, E&M0570, E&M0620	E&M0670								
E&M0650	Hydraulic Tests of Pipeworks	153	60	02/01/13 A	30/01/14	02/01/13 A	15/06/13	-229d	E&M0590, YSW08302	E&M0690								
E&M0660	Cabling Works	15	42	04/02/15 A	11/08/15	04/02/15 A	21/05/13	-812d	E&M0320, E&M0325, E&M0660, E&M0305, E&M0325, E&M0620	E&M0690								
E&M0670	Insulation Tests of Cables and Cable Termination	26	30	11/04/15 A	29/08/15	11/04/15 A	08/06/13	-812d	E&M0510, E&M0520, E&M0570, E&M0580, E&M0590, E&M0600, E&M0605, E&M0610, E&M0630, E&M0640, E&M0650, E&M0670, YSW0380, YSW08301, YSW1530,	E&M0700								
E&M0680	Energization	1	100	02/04/15 A	03/04/15 A	02/04/15 A	03/04/15 A		E&M0330, E&M0690	E&M0730, KD0040								
E&M0690	Functional and Performance Tests of Equipment	35	45	25/03/15 A	17/09/15	25/03/15 A	27/06/13 *	-812d	E&M0700	KD0132								
E&M0700	T&C Period	137	0	08/11/15	24/03/16	12/12/13	27/04/14	-697d										
E&M0730	Trial Operation Period	413	0	24/03/16	20/10/17	28/04/14	14/06/15	-697d										

**Sok Kwu Wan**

Preliminary																		
SKW0250	Approval of Environmental Team	16	100	17/05/10 A	01/06/10 A	17/05/10 A	01/06/10 A		KD0020	SKW0260								
SKW0260	Baseline monitoring (Air & Noise)	14	100	02/06/10 A	15/06/10 A	02/06/10 A	15/06/10 A		SKW0250	SKW0242, SKW0265, SKW0592,								
SKW0265	Baseline Monitoring Submission (A & N)	14	100	16/06/10 A	08/07/10 A	16/06/10 A	08/07/10 A		SKW0260	SKW0242, SKW0592, SKW0681,								

**Section W3 - Footpath Diversion in Portion G**

Civil & Geotechnical Works																		
SKW0240	Site Clearance	21	100	17/05/10 A	06/06/10 A	17/05/10 A	06/06/10 A			SKW0241								
SKW0241	Initial Survey	9	100	07/06/10 A	15/06/10 A	07/06/10 A	15/06/10 A		SKW0240	SKW0242								
SKW0242	Retaining Wall Bay 0-10 (Incl. VO. 001A)	177	100	30/06/10 A	23/12/10 A	30/06/10 A	23/12/10 A		SKW0241, SKW0260, SKW0265	SKW0461								
SKW0461	Utilities Laying and Diversion	70	100	24/12/10 A	03/03/11 A	24/12/10 A	03/03/11 A		SKW0242	SKW0471								
SKW0471	Concreting for Pavement	7	100	04/03/11 A	10/03/11 A	04/03/11 A	10/03/11 A		SKW0461	SKW0481								
SKW0481	Footpath Diversion - Stage 1	14	100	11/03/11 A	24/03/11 A	11/03/11 A	24/03/11 A		SKW0471	KD0050, SKW04811, SKW0491								
SKW04811	Excavate for FP transition at CH0-35 & CH130-141	37	100	25/03/11 A	30/04/11 A	25/03/11 A	30/04/11 A		SKW0481	SKW04821								
SKW04821	Construction of Drainage outfall near bay 10	3	100	01/05/11 A	03/05/11 A	01/05/11 A	03/05/11 A		SKW04811	SKW04831								
SKW04831	Cable diversion by HEC	26	100	04/05/11 A	29/05/11 A	04/05/11 A	29/05/11 A		SKW04821	SKW04841								
SKW04841	Diversion of Ducting and Drawpit by PCCW	12	100	20/05/11 A	31/05/11 A	20/05/11 A	31/05/11 A		SKW04831	SKW04851								
SKW04851	Soil backfilling behind FP retaining wall	14	100	01/06/11 A	14/06/11 A	01/06/11 A	14/06/11 A		SKW04841	SKW04861								
SKW04861	Concreting for footpath pavement	7	100	15/06/11 A	21/06/11 A	15/06/11 A	21/06/11 A		SKW04851	SKW04871								
SKW04871	Relocation of Temp Safety Fence at SKW STW A-G	57	100	22/06/11 A	17/08/11 A	22/06/11 A	17/08/11 A		SKW04861	SKW04881								
SKW04881	Disposal of excavation material at A-G SKW STW	138	100	18/08/11 A	02/01/12 A	18/08/11 A	02/01/12 A		SKW04871	SKW04885								
SKW04885	Footpath Diversion - Stage 2	7	100	03/01/12 A	09/01/12 A	03/01/12 A	09/01/12 A		SKW04881	SKW1261								
SKW0491	Removal of Haul Road after SKW STW	7	0	08/10/14	14/10/14	29/05/15	04/06/15	233d	KD0090, SKW0481, SKW1401	SKW0501								

Start date	05/05/10
Finish date	20/10/17
Data date	30/11/13
Run date	04/03/14
Page number	6A
© Primavera Systems, Inc.	

<ul style="list-style-type: none"> <li><span style="color: green;">█</span> Early bar</li> <li><span style="color: blue;">█</span> Progress bar</li> <li><span style="color: red;">█</span> Critical bar</li> <li><span style="color: grey;">█</span> Summary bar</li> <li><span style="color: blue;">▲</span> Progress point</li> <li><span style="color: red;">▼</span> Critical point</li> <li><span style="color: blue;">◆</span> Summary point</li> <li><span style="color: orange;">◆</span> Start milestone point</li> <li><span style="color: orange;">◆</span> Finish milestone point</li> </ul>	<p><b>Leader Civil Engineering Corp. Ltd.</b>  <b>Contract No. DC/2009/13</b>  <b>Construction of Sewage Treatment Works at YSW &amp; SKW</b>  <b>3-month Rolling Programme (Feb 2014 - April 201)</b></p>	<table border="1"> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> <tr> <td>31/01/14</td> <td>Revision 0</td> <td>RH</td> <td>VC</td> </tr> <tr> <td> </td> <td> </td> <td> </td> <td> </td> </tr> <tr> <td> </td> <td> </td> <td> </td> <td> </td> </tr> </table>	Date	Revision	Checked	Approved	31/01/14	Revision 0	RH	VC								
Date	Revision	Checked	Approved															
31/01/14	Revision 0	RH	VC															

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	OCT	2013 NOV	DEC	JAN	2014 FEB	MAR
SKW0501	Concreting for no-fine concrete	14	0	08/10/14	21/10/14	29/05/15	11/06/15	233d	SKW0491	SKW0511						
SKW0511	Wall Tie & Stone Facing	14	0	22/10/14	04/11/14	12/06/15	25/06/15	233d	SKW0501	SKW0521						
SKW0521	Gabion Wall & Geotextile	30	0	05/11/14	04/12/14	26/06/15	25/07/15	233d	SKW0511	SKW0531						
SKW0531	Installation of Flower Pot	7	0	05/12/14	11/12/14	26/07/15	01/08/15	233d	SKW0521	SKW0541						
SKW0541	Completion of Outstanding Works	42	0	12/12/14	22/01/15	02/08/15	12/09/15	233d	SKW0531	KD0125						

**Section W4 - Slope Works in Portions H & I**

Geotechnical Works											OCT	2013 NOV	DEC	JAN	2014 FEB	MAR
SKW0588	Construct scaffolding access	30	100	15/06/10 A	14/07/10 A	15/06/10 A	14/07/10 A		KD0020	SKW0590						
SKW0590	Site Clearance for Slope	100	100	15/07/10 A	22/10/10 A	15/07/10 A	22/10/10 A		SKW0588	SKW0591						
SKW0591	Initial Survey for Slope	28	100	21/09/10 A	18/10/10 A	21/09/10 A	18/10/10 A		SKW0590	SKW0592						
SKW0592	Temporary Rockfall fence at ex. Footpath	43	100	31/08/10 A	12/10/10 A	31/08/10 A	12/10/10 A		SKW0260, SKW0265, SKW0591	SKW05931						
SKW05931	Construction of Haul Road (To +30mPD)	50	100	03/09/10 A	22/10/10 A	03/09/10 A	22/10/10 A		SKW0592	SKW05932						
SKW05932	Construction of Haul Road (To +42.5mPD)	68	100	23/10/10 A	29/12/10 A	23/10/10 A	29/12/10 A		SKW05931	SKW059322						
SKW059321	Removal of Boulders (IBG 1 - 119, SI No. 11B)	121	100	03/11/10 A	03/03/11 A	03/11/10 A	03/03/11 A			SKW059411						
SKW059322	Add. Site Invest. Works (VO. No. 9,12 & 16)	174	100	11/01/11 A	03/07/11 A	11/01/11 A	03/07/11 A		SKW05932	SKW059341						
SKW059323	Revised Profile at West Slope (+56 to +42.5mPD)	1	100	17/03/11 A	17/03/11 A	17/03/11 A	17/03/11 A			SKW059324						
SKW059324	Construction of Haul Road (+42.5 to +56mPD)	12	100	18/03/11 A	29/03/11 A	18/03/11 A	29/03/11 A		SKW059323	SKW059325						
SKW059325	Removal of Boulders (IBG 120-139, SI No. 11C)	17	100	30/03/11 A	15/04/11 A	30/03/11 A	15/04/11 A		SKW059324	SKW05933						
SKW05933	West Slope Cutting (+56mPD to +42.5mPD)	2	100	16/04/11 A	17/04/11 A	16/04/11 A	17/04/11 A		SKW059325	SKW059331						
SKW059331	Removal of Boulders (IBG 140-189, SI No. 11D)	45	100	18/04/11 A	01/06/11 A	18/04/11 A	01/06/11 A		SKW05933	SKW05934						
SKW05934	West Slope Cutting (+42.5mPD to +35mPD)	32	100	02/06/11 A	03/07/11 A	02/06/11 A	03/07/11 A		SKW059331	SKW059341						
SKW059341	Revised Profile at West Slope (+20 to +4.8mPD)	1	100	04/07/11 A	04/07/11 A	04/07/11 A	04/07/11 A		SKW059322, SKW05934	SKW05935						
SKW05935	West Slope Cutting (+35mPD to +27.5mPD)	83	100	08/07/11 A	28/09/11 A	08/07/11 A	28/09/11 A		SKW059341	SKW05936						
SKW05936	West Slope Cutting (+27.5mPD to +20mPD)	61	100	29/09/11 A	28/11/11 A	29/09/11 A	28/11/11 A		SKW05935	SKW05937						
SKW05937	West Slope Cutting (+20mPD to +12.5mPD)	39	100	29/11/11 A	06/01/12 A	29/11/11 A	06/01/12 A		SKW05936	SKW05938						
SKW05938	West Slope Cutting (+12.5mPD to +4.8mPD)	90	100	07/01/12 A	27/03/12 A	07/01/12 A	27/03/12 A		SKW05937	KD0060, SKW1261, SKW1311,						
SKW05941	Slope Stormwater Drainage	300	100	28/03/12 A	25/05/12 A	28/03/12 A	25/05/12 A		KD0060	SKW05942						
SKW059411	East Slope Cutting (+50mPD to +42.5mPD)	72	100	04/03/11 A	14/05/11 A	04/03/11 A	14/05/11 A		SKW059321	SKW059412						
SKW059412	East Slope Cutting (+42.5mPD to +35mPD)	82	100	15/05/11 A	04/08/11 A	15/05/11 A	04/08/11 A		SKW059411	SKW059413						
SKW059413	East Slope Cutting (+35mPD to +27.5mPD)	55	100	05/08/11 A	28/09/11 A	05/08/11 A	28/09/11 A		SKW059412	SKW059414						
SKW059414	East Slope Cutting (+27.5mPD to +20mPD)	61	100	29/09/11 A	28/11/11 A	29/09/11 A	28/11/11 A		SKW059413	SKW059415						
SKW059415	East Slope Cutting (+20mPD to +12.5mPD)	39	100	29/11/11 A	06/01/12 A	29/11/11 A	06/01/12 A		SKW059414	SKW059416						
SKW059416	East Slope Cutting (+12.5mPD to +4.8mPD)	81	100	07/01/12 A	27/03/12 A	07/01/12 A	27/03/12 A		SKW059415	KD0060, SKW1311, SKW1371						
SKW05942	Slope Miscellaneous Works	61	100	26/05/12 A	31/07/12 A	26/05/12 A	31/07/12 A		SKW05941	SKW05943, SKW0595						
SKW05943	Buttress & surface Protection (SI No. 31)	60	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		SKW05942	SKW05944						
SKW05944	Slope Treatment (SI. No. 36)	60	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		SKW05943	SKW05945						
SKW05945	Rock Slope Treatment (SI. No. 68)	60	100	01/08/12 A	30/09/12 A	01/08/12 A	30/09/12 A		SKW05944	SKW05946						
SKW05946	Rock Slope Treatment (SI. No. 98)	60	100	10/09/12 A	28/02/13 A	10/09/12 A	28/02/13 A		SKW05945	SKW05947						
SKW05947	Rock Slope Treatment (SI. No. 115)	60	100	01/11/12 A	28/02/13 A	01/11/12 A	28/02/13 A		SKW05946	KD0135						
SKW05948	Soil Nailing Works (VO. No. 52)	300	100	10/02/12 A	28/02/13 A	10/02/12 A	28/02/13 A			SKW05963						
SKW0595	Rock Meshing	60	0	30/11/13	28/01/14	07/08/15	05/10/15	615d	SKW05942, SKW05972	KD0165						
SKW05963	Determine Alignment & Foundation Design of RFB	120	100	10/02/12 A	08/06/12 A	10/02/12 A	08/06/12 A		SKW05948	SKW059631, SKW05964,						
SKW059631	GEO Approval of Foundation Design	70	100	09/06/12 A	31/07/12 A	09/06/12 A	31/07/12 A		SKW05963	SKW05968						
SKW05964	Fabrication & Shipping of RFB Material	180	100	09/06/12 A	30/11/12 A	09/06/12 A	30/11/12 A		SKW05963	SKW05972						
SKW05965	Site clearance & Formation of access	62	100	09/06/12 A	31/07/12 A	09/06/12 A	31/07/12 A		SKW05963	SKW05967						
SKW05967	Plant mobilization	14	100	02/01/13 A	15/01/13 A	02/01/13 A	15/01/13 A		SKW05965	SKW05968						
SKW05968	Construction of anchors & pull out test	180	100	16/01/13 A	17/08/13 A	16/01/13 A	17/08/13 A		SKW059631, SKW05967	SKW05969						
SKW05969	Construction of Foundation	120	100	11/07/13 A	23/08/13 A	11/07/13 A	23/08/13 A		SKW05968	SKW05970						
SKW05970	Proof Load Test	60	100	31/07/13 A	28/09/13 A	31/07/13 A	28/09/13 A		SKW05969	SKW05971						
SKW05971	Transportation of Material (To the slope crest)	30	100	31/07/13 A	29/08/13 A	31/07/13 A	29/08/13 A		SKW05970	SKW05972						
SKW05972	Installation of Flexible barrier	90	100	31/07/13 A	28/10/13 A	31/07/13 A	28/10/13 A		SKW05964, SKW05971	KD0165, SKW0595						

**Section W5 - P.S. No. 1 in Portion D**

YSW16605	Construct UU & pipes along sea side (Grid D-Q)	60	80	20/11/13 A	09/02/14	20/11/13 A	28/11/13	-73d	YSW16604	YSW16702, YSW1700						
----------	--	----	----	------------	----------	------------	----------	------	----------	-------------------	--	--	--	--	--	--

Civil & Geotechnical Works											OCT	2013 NOV	DEC	JAN	2014 FEB	MAR
SKW0651	Site Clearance	7	100	17/05/10 A	23/05/10 A	17/05/10 A	23/05/10 A		KD0020	SKW0652						

Start date	05/05/10	Early bar
Finish date	20/10/17	Progress bar
Data date	30/11/13	Critical bar
Run date	04/03/14	Summary bar
Page number	7A	Progress point
© Primavera Systems, Inc.		Critical point
		Summary point
		Start milestone point
		Finish milestone point

**Leader Civil Engineering Corp. Ltd.**  
**Contract No. DC/2009/13**  
**Construction of Sewage Treatment Works at YSW & SKW**  
**3-month Rolling Programme (Feb 2014 - April 2015)**

Date	Revision	Checked	Approved
31/01/14	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013							
											OCT	NOV	DEC	JAN	2014 FEB	MAR		
SKW0652	Initial Survey	7	100	24/05/10 A	30/05/10 A	24/05/10 A	30/05/10 A		SKW0651	SKW0661, SKW0681								
SKW0661	Transplantation for uncommon vegetation	30	100	31/05/10 A	29/06/10 A	31/05/10 A	29/06/10 A		SKW0652	SKW0681								
SKW0681	Excavate to lower the working platform to +3mPD	49	100	30/06/10 A	17/08/10 A	30/06/10 A	17/08/10 A		SKW0260, SKW0265, SKW0652,	SKW0691								
SKW0691	ELS to +2.2mPD	40	100	18/08/10 A	26/09/10 A	18/08/10 A	26/09/10 A		SKW0681	SKW0721								
SKW0721	Excavate to formation	270	100	17/09/10 A	13/06/11 A	17/09/10 A	13/06/11 A		SKW0691	SKW0741								
SKW0722	Construction of Manholes (VO. No. 21A)	107	90	28/10/13 A	08/05/14	28/10/13 A	08/07/14	62d	E&M11800	E&M3360								
<b>Structural Works</b>																		
SKW0741	RC Works for Structure	240	100	14/06/11 A	08/02/12 A	14/06/11 A	08/02/12 A		SKW0721	KD0070, SKW0841								
SKW0841	ABWF works	60	100	09/02/12 A	08/04/12 A	09/02/12 A	08/04/12 A		SKW0741	E&M1101, E&M1102, E&M1103,								
SKW0861	300mm U-channel & 675mm Step Channel	30	20	26/01/14 A	21/05/14	26/01/14 A	05/10/15	502d	E&M11800, SKW0841	KD0165								
<b>E&amp;M Works (PS1)</b>																		
<b>Submission &amp; Delivery</b>																		
E&M1001	Submission of Pumps	198	100	17/05/10 A	24/02/11 A	17/05/10 A	24/02/11 A		KD0020	E&M1011								
E&M1002	Submission of Gen-Set	198	100	17/05/10 A	24/02/11 A	17/05/10 A	24/02/11 A			E&M1012								
E&M1003	Submission of DeO System	198	100	17/05/10 A	16/07/13 A	17/05/10 A	16/07/13 A			E&M1013								
E&M1004	Submission of LV SB & MCC	180	100	17/05/10 A	09/01/12 A	17/05/10 A	09/01/12 A			E&M1014								
E&M1005	Submission of Instrumentation	243	100	17/05/10 A	12/03/12 A	17/05/10 A	12/03/12 A			E&M1015								
E&M1006	Submission of FS System	243	100	17/05/10 A	30/09/12 A	17/05/10 A	30/09/12 A			E&M1016								
E&M1007	Submission of BS System	243	97	17/05/10 A	07/12/13	17/05/10 A	21/02/14	76d		E&M1017								
E&M1011	Delivery of Pumps	150	100	24/02/11 A	21/07/11 A	24/02/11 A	21/07/11 A		E&M1001	E&M1101								
E&M1012	Delivery of Gen-Set	150	100	24/02/11 A	23/09/11 A	24/02/11 A	23/09/11 A		E&M1002	E&M1102								
E&M1013	Delivery of DeO System	150	100	11/07/11 A	28/10/11 A	11/07/11 A	28/10/11 A		E&M1003	E&M1103								
E&M1014	Delivery of LV SB & MCC	150	100	01/06/12 A	31/07/12 A	01/06/12 A	31/07/12 A		E&M1004	E&M1104								
E&M1015	Delivery of Instrumentation	90	100	01/11/11 A	03/11/11 A	01/11/11 A	03/11/11 A		E&M1005	E&M1105								
E&M1016	Delivery of FS Equipment	107	80	01/12/11 A	21/12/13	01/12/11 A	20/02/14	62d	E&M1006	E&M1106								
E&M1017	Delivery of BS Equipment	107	80	15/11/11 A	28/12/13	15/11/11 A	14/03/14	76d	E&M1007	E&M1107								
<b>Installation, T&amp;C</b>																		
E&M1101	Install Pumps	55	90	02/10/12 A	05/12/13	02/10/12 A	23/03/14	108d	E&M1011, SKW0841	E&M1110, E&M1140								
E&M1102	Install Gen Set	55	100	02/10/12 A	05/05/13 A	02/10/12 A	05/05/13 A		E&M1012, SKW0841	E&M1110, E&M1140								
E&M1103	Install DeO System	55	95	03/12/12 A	02/12/13	03/12/12 A	23/03/14	111d	E&M1013, SKW0841	E&M1110, E&M1140								
E&M1104	Install LV SB & MCC	55	100	02/01/13 A	26/03/13 A	02/01/13 A	26/03/13 A		E&M1014, SKW0841	E&M1140								
E&M1105	Install Instrumentation	55	48	01/11/12 A	28/12/13	01/11/12 A	23/03/14	85d	E&M1015, SKW0841	E&M1140								
E&M1106	Install FS Equipment	55	45	02/10/12 A	20/01/14	02/10/12 A	23/03/14	62d	E&M1016, SKW0841	E&M1130, E&M1140								
E&M1107	Install BS Equipment	55	85	02/10/12 A	05/01/14	02/10/12 A	23/03/14	76d	E&M1017, SKW0841	E&M1110, E&M1140								
E&M1110	Install Valves, Pipes & Fittings	46	100	02/01/13 A	27/03/13 A	02/01/13 A	27/03/13 A		E&M1101, E&M1102, E&M1103,	E&M1120								
E&M1130	Form 501 Submission to FSD	28	0	20/01/14	17/02/14	01/04/14	29/04/14	71d	E&M1106	E&M11800								
E&M1140	Cabling Works	43	80	21/05/13 A	29/01/14	21/05/13 A	31/03/14	62d	E&M1101, E&M1102, E&M1103,	E&M1150								
E&M1150	Insulation Tests of Cables and Cable Termination	7	80	25/06/13 A	30/01/14	25/06/13 A	02/04/14	62d	E&M1140	E&M1160								
E&M1160	Engergization	3	100	01/07/13 A	02/08/13 A	01/07/13 A	02/08/13 A		E&M1150	E&M1170								
E&M1170	Functional and Performance Tests of Equipment	30	10	02/01/13 A	26/02/14	02/01/13 A	29/04/14	62d	E&M1160	E&M11800								
E&M11800	Commissioning Test	60	0	26/02/14	27/04/14	29/04/14	28/06/14	62d	E&M0350, E&M1120, E&M1130,	SKW0722, SKW0861								

Start date	05/05/10	<span style="color: green;">■</span> Early bar
Finish date	20/10/17	<span style="color: blue;">■</span> Progress bar
Data date	30/11/13	<span style="color: red;">■</span> Critical bar
Run date	04/03/14	<span style="color: grey;">■</span> Summary bar
Page number	8A	<span style="color: blue;">▲</span> Progress point
c Primavera Systems, Inc.		<span style="color: red;">▼</span> Critical point
		<span style="color: blue;">◆</span> Summary point
		<span style="color: orange;">◆</span> Start milestone point
		<span style="color: gold;">◆</span> Finish milestone point

**Leader Civil Engineering Corp. Ltd.**  
**Contract No. DC/2009/13**  
**Construction of Sewage Treatment Works at YSW & SKW**  
**3-month Rolling Programme (Feb 2014 - April 201)**

Date	Revision	Checked	Approved
31/01/14	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	Timeline						
											OCT	2013 NOV	DEC	JAN	2014 FEB	MAR	
SKW1531	Extent village sewers S163.1 & S164.1	34	100	30/11/12 A	10/01/13 A	30/11/12 A	10/01/13 A		SKW15111	SKW1581							
SKW1581	Construct Manhole no. S163 & S164	34	100	11/01/13 A	28/02/13 A	11/01/13 A	28/02/13 A		SKW1531	KD0135, SKW15112							
<b>Structural Works</b>																	
SKW0971	Structural Works (Phase 1)	245	100	11/06/11 A	10/02/12 A	11/06/11 A	10/02/12 A		SKW0951	KD0080, SKW1021							
SKW1021	Structural Works (Phase 2)	42	100	11/02/12 A	23/03/12 A	11/02/12 A	23/03/12 A		SKW0971	SKW1061, SKW1081, SKW1491							
SKW1061	ABWF Works	90	100	24/03/12 A	21/06/12 A	24/03/12 A	21/06/12 A		SKW1021	E&M2101, E&M2102, E&M2103,							
SKW1081	375mm U-channel/catchpits/outfall	30	100	22/06/12 A	31/01/13 A	22/06/12 A	31/01/13 A		SKW1021, SKW1061	KD0155, SKW0961							
<b>E&amp;M Works (PS2)</b>																	
<b>Submission &amp; Delivery</b>																	
E&M2001	Submission of Pumps	198	100	17/05/10 A	24/02/11 A	17/05/10 A	24/02/11 A		KD0020	E&M2011							
E&M2002	Submission of Gen-Set	198	100	17/05/10 A	24/02/11 A	17/05/10 A	24/02/11 A			E&M2012							
E&M2003	Submission of DeO System	198	100	17/05/10 A	11/07/11 A	17/05/10 A	11/07/11 A			E&M2013							
E&M2004	Submission of LV SB & MCC	271	100	17/05/10 A	30/06/12 A	17/05/10 A	30/06/12 A			E&M2014							
E&M2005	Submission of Instrumentation	243	100	17/05/10 A	30/06/12 A	17/05/10 A	30/06/12 A			E&M2015							
E&M2006	Submission of FS System	243	97	17/05/10 A	07/12/13	17/05/10 A	12/09/12	-450d		E&M2016							
E&M2007	Submission of BS System	243	97	17/05/10 A	07/12/13	17/05/10 A	04/10/12	-428d		E&M2017							
E&M2011	Delivery of Pumps	150	100	24/02/11 A	21/07/11 A	24/02/11 A	21/07/11 A		E&M2001	E&M2101							
E&M2012	Delivery of Gen-Set	150	100	24/02/11 A	23/09/11 A	24/02/11 A	23/09/11 A		E&M2002	E&M2102							
E&M2013	Delivery of DeO System	150	100	11/07/11 A	28/10/11 A	11/07/11 A	28/10/11 A		E&M2003	E&M2103							
E&M2014	Delivery of LV SB & MCC	150	100	29/02/12 A	31/07/12 A	29/02/12 A	31/07/12 A		E&M2004	E&M2104							
E&M2015	Delivery of Instrumentation	90	100	21/06/11 A	03/11/11 A	21/06/11 A	03/11/11 A		E&M2005	E&M2105							
E&M2016	Delivery of FS Equipment	107	80	01/12/11 A	28/12/13	01/12/11 A	04/10/12	-450d	E&M2006	E&M0350, E&M2106							
E&M2017	Delivery of BS Equipment	107	80	15/01/11 A	28/12/13	15/01/11 A	26/10/12	-428d	E&M2007	E&M2107							
<b>Installation, T&amp;C</b>																	
E&M2101	Install Pumps	55	80	02/10/12 A	10/12/13	02/10/12 A	12/01/13	-332d	E&M2011, SKW1061	E&M2110							
E&M2102	Install Gen Set	55	100	01/09/12 A	05/05/13 A	01/09/12 A	05/05/13 A		E&M2012, SKW1061	E&M2110							
E&M2103	Install DeO System	55	90	03/12/12 A	05/12/13	03/12/12 A	12/01/13	-327d	E&M2013, SKW1061	E&M2110							
E&M2104	Install LV SB & MCC	55	100	02/01/13 A	31/01/13 A	02/01/13 A	31/01/13 A		E&M2014, SKW1061	E&M2140							
E&M2105	Install Instrumentation	55	40	31/05/13 A	01/01/14	31/05/13 A	03/11/12	-424d	E&M2015, SKW1061	E&M2140							
E&M2106	Install FS Equipment	55	45	02/10/12 A	27/01/14	02/10/12 A	03/11/12	-450d	E&M2016, SKW1061	E&M2140							
E&M2107	Install BS Equipment	55	85	01/09/12 A	05/01/14	01/09/12 A	03/11/12	-428d	E&M2017, SKW1061	E&M2110, E&M2140							
E&M2110	Install Valves, Pipes & Fittings	46	100	02/01/13 A	31/01/13 A	02/01/13 A	31/01/13 A		E&M2101, E&M2102, E&M2103,	E&M2120							
E&M2120	Hydraulic Test of Pipeworks	7	100	02/01/13 A	31/01/13 A	02/01/13 A	31/01/13 A		E&M2110	E&M2130							
E&M2130	Form 501 Submission to FSD	28	0	05/01/14	02/02/14	13/01/13	09/02/13	-358d	E&M2120	KD0155							
E&M2140	Cabling Works	43	80	01/02/13 A	05/02/14	01/02/13 A	12/11/12	-450d	E&M2104, E&M2105, E&M2106,	E&M2150							
E&M2150	Insulation Tests of Cables and Cable Termination	7	60	01/02/13 A	08/02/14	01/02/13 A	14/11/12	-450d	E&M2140	E&M2160							
E&M2160	Energization	3	100	01/02/13 A	25/03/13 A	01/02/13 A	25/03/13 A		E&M2150	E&M2170							
E&M2170	Functional and Performance Tests of Equipment	30	10	15/01/13 A	07/03/14	15/01/13 A	11/12/12	-450d	E&M2160	E&M2180							
E&M2180	Commissioning Test	60	0	07/03/14	06/05/14	12/12/12	09/02/13	-450d	E&M0350, E&M2170	KD0155							
<b>Section W7 - SKW STW, Sewer and Submarine Outfall</b>																	
<b>Submarine Outfall</b>																	
SKW1130	Approval of IHS Consultant	180	100	17/05/10 A	27/08/10 A	17/05/10 A	27/08/10 A			SKW1131							
SKW1131	Hydrographical Survey (SKW)	300	100	01/02/11 A	28/02/11 A	01/02/11 A	28/02/11 A		KD0020, SKW1130	SKW1231							
SKW1141	Baseline Monitoring (Water)	213	100	27/07/10 A	31/12/10 A	27/07/10 A	31/12/10 A		SKW0260, SKW0265	SKW1151							
SKW1151	Set up Temporary Working Platform	90	100	15/06/11 A	30/09/11 A	15/06/11 A	30/09/11 A		PRE0090, SKW1141	SKW1171							
SKW1171	ELS for HDD Set-up (SKW)	90	100	01/09/11 A	30/09/11 A	01/09/11 A	30/09/11 A		SKW1151	SKW1181							
SKW1181	Mobilization of HDD plant & equipment to SKW	8	100	06/01/12 A	07/01/12 A	06/01/12 A	07/01/12 A		SKW1171, YSW0360	SKW1191							
SKW1191	Setting up at drillhole location	7	100	09/01/12 A	14/01/12 A	09/01/12 A	14/01/12 A		SKW1181	SKW1201							
SKW1201	Drill pilot hole and reaming hole - NS280 - 750m	33	100	16/01/12 A	16/02/12 A	16/01/12 A	16/02/12 A		SKW1191	SKW1211							
SKW1211	Receiving Pit for HDD (SKW)	13	100	16/01/12 A	29/02/12 A	16/01/12 A	29/02/12 A		SKW1201	SKW1221							
SKW1221	Installation of NS280 HDPE 450mm dia. pipe	61	100	31/03/12 A	30/04/12 A	31/03/12 A	30/04/12 A		SKW1211	KD0090, SKW1231, SKW1441							
SKW1231	Removal of Receiving Platform	50	100	01/05/12 A	19/06/12 A	01/05/12 A	19/06/12 A		SKW1131, SKW1221	SKW1241							
SKW1241	Dredging of MD for Diffuser (PS CL 1.122(3))	16	100	20/06/12 A	05/07/12 A	20/06/12 A	05/07/12 A		SKW1231	E&M3359, SKW1251							
SKW1251	Diffuser Construction	77	100	01/09/12 A	16/11/12 A	01/09/12 A	16/11/12 A		SKW1241	SKW1431							
SKW1431	Removal of silt curtain	1	100	17/11/12 A	17/11/12 A	17/11/12 A	17/11/12 A		SKW1251	KD0090, SKW1440, YSW0365							
SKW1440	Sewer of Outfall Chamber to connection pit VO37A	90	95	31/12/12 A	04/12/13	31/12/12 A	08/05/14	155d	SKW1431	SKW1441							

Start date	05/05/10
Finish date	20/10/17
Data date	30/11/13
Run date	04/03/14
Page number	9A
© Primavera Systems, Inc.	

Early bar	Progress bar	Critical bar	Summary bar
▲ Progress point	▼ Critical point	◆ Summary point	◆ Start milestone point
			◆ Finish milestone point

**Leader Civil Engineering Corp. Ltd.**  
**Contract No. DC/2009/13**  
**Construction of Sewage Treatment Works at YSW & SKW**  
**3-month Rolling Programme (Feb 2014 - April 201)**

Date	Revision	Checked	Approved
31/01/14	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2014					
											OCT	NOV	DEC	JAN	FEB	MAR
SKW1441	Sewer of Connection Pit to Outfall VO45	177	85	05/06/13 A	30/12/13	05/06/13 A	03/06/14	155d	SKW1221, SKW1440	E&M3359, KD0090	Sewer of Connection Pit to Outfall VO45					
<b>SKW STW</b>																
<b>Submission &amp; Delivery (E&amp;M)</b>																
E&M3010	Delivery of MBR M.M. - 1st shipment for Temp STP	150	100	24/02/11 A	17/10/11 A	24/02/11 A	17/10/11 A		E&M0160	E&M3170						
E&M3030	Delivery of Grit Removal Equipment	180	100	10/10/11 A	29/12/11 A	10/10/11 A	29/12/11 A		E&M0150	E&M3190						
E&M3060	Delivery of Fine Screens	136	100	12/09/11 A	30/11/11 A	12/09/11 A	30/11/11 A		E&M0120	E&M3210						
E&M3070	Delivery of Pumps	136	100	23/06/11 A	05/09/11 A	23/06/11 A	05/09/11 A		E&M0130	E&M3220						
E&M3080	Delivery of Submersible Mixers	180	100	26/07/11 A	17/11/11 A	26/07/11 A	17/11/11 A		E&M0140	E&M3230						
E&M3090	Delivery of Sludge Dewatering Equipment	210	70	01/09/11 A	31/01/14	01/09/11 A	11/01/14	-20d	E&M0170	E&M3240	Delivery of Sludge Dewatering Equipment					
E&M3100	Delivery of Valves, Pipes & Fittings	180	70	30/08/11 A	22/01/14	30/08/11 A	19/11/13	-64d	E&M0180	E&M3250	Delivery of Valves, Pipes & Fittings					
E&M3110	Delivery of Penstocks	180	100	12/08/11 A	24/12/11 A	12/08/11 A	24/12/11 A		E&M0190	E&M3260						
E&M3130	Delivery of instruments	180	100	21/06/11 A	03/11/11 A	21/06/11 A	03/11/11 A		E&M0200	E&M3270						
E&M3140	Delivery of MCC LVSB	180	0	01/12/13	30/05/14	07/04/13	03/10/13	-239d	E&M0210	E&M3261						
E&M3150	Delivery of BS Equipment	180	8	03/07/12 A	19/06/14	03/07/12 A	04/12/13	-196d	E&M0220	E&M3291						
E&M3160	Delivery of FS Equipment	180	5	30/06/12 A	06/07/14	30/06/12 A	23/12/13	-195d	E&M0230	E&M0340, E&M3300						
<b>Construction of Grid A-G</b>																
SKW1261	Excavate for SKW STW Structure (Grid A-G)	164	100	28/03/12 A	31/08/12 A	28/03/12 A	31/08/12 A		SKW04885, SKW05938	SKW1271, SKW1371						
SKW1271	55 M3 Fire Sprinkle Water Tank (FL +0.9 mPD)	36	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		SKW1261	SKW1281						
SKW1281	Ground Floor Slab (Grid A-G)	46	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		SKW1271	SKW1291						
SKW1291	Columns & Walls to 1/F & 1/F Slab (Grid A-G)	50	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		SKW1281	KD0090, SKW1301						
SKW1301	Columns & Walls to R/F & R/F Slab (Grid A-G)	50	100	01/09/12 A	31/01/13 A	01/09/12 A	31/01/13 A		SKW1291	E&M3261, E&M3291, E&M3311,						
SKW1411	ABWF Works	105	65	01/02/13 A	05/01/14	01/02/13 A	19/06/13	-200d	SKW1301	E&M3261, E&M3291, E&M3311,	ABWF Works					
<b>Construction of Grid G-N</b>																
SKW1311	Excavate for SKW STW Structure (Grid G-N)	90	100	28/03/12 A	25/06/12 A	28/03/12 A	25/06/12 A		SKW05938, SKW059416	SKW1321, SKW1371						
SKW1321	Equalization Tank no.1 & 2 with base slabs (-2.1	42	100	26/06/12 A	30/09/12 A	26/06/12 A	30/09/12 A		SKW1311	SKW1331						
SKW1331	Columns & Walls from B/S to G/F Slab (Grid G-N)	35	100	01/09/12 A	30/09/12 A	01/09/12 A	30/09/12 A		SKW1321	SKW1341						
SKW1341	Ground Floor Slab (Grid G-N)	35	100	01/09/12 A	17/12/12 A	01/09/12 A	17/12/12 A		SKW1331	SKW1351						
SKW1351	Columns & Walls to 1/F & 1/F Slab (Grid G-N)	28	100	01/11/12 A	15/01/13 A	01/11/12 A	15/01/13 A		SKW1341	SKW1361						
SKW1361	Columns & Walls to R/F & R/F Slab (Grid G-N)	35	100	01/11/12 A	03/08/13 A	01/11/12 A	03/08/13 A		SKW1351	SKW1451	Slab (Grid G-N)					
SKW1451	ABWF Works	54	65	05/06/13 A	18/12/13	05/06/13 A	17/05/13	-215d	SKW1361	E&M3170, E&M3190, E&M3210, E&M3291, E&M3300, SKW1391,	ABWF Works					
<b>Construction of Grid N-T</b>																
SKW1371	Excavate for SKW STW Structure (Grid N-T)	97	100	03/07/12 A	25/01/13 A	03/07/12 A	25/01/13 A		SKW05938, SKW059416, SKW1261,	SKW1381						
SKW1381	Ground Floor Slabs include MBR Tank (Grid N-T)	58	100	02/10/12 A	31/01/13 A	02/10/12 A	31/01/13 A		SKW1371	SKW1391						
SKW1391	Columns & Walls to 1/F & 1/F Slab (Grid N-T)	35	100	31/05/13 A	05/07/13 A	31/05/13 A	05/07/13 A		SKW1381, SKW1451	SKW1401						
SKW1401	Columns & Walls to R/F & R/F Slab (Grid N-T)	35	100	03/07/13 A	15/09/13 A	03/07/13 A	15/09/13 A		SKW1391	E&M3240, SKW0491, SKW1421	Columns & Walls to R/F & R/F Slab (Grid N-T)					
SKW1421	ABWF Works	60	45	06/08/13 A	20/01/14	06/08/13 A	19/06/13	-215d	SKW1401	E&M3240, SKW1551	ABWF Works					
SKW1551	Drainage (SSMH1-SSMH7)	35	0	20/01/14	24/02/14	20/06/13	24/07/13	-215d	SKW1411, SKW1421, SKW1451	SKW1561	Drainage (SSMH1)					
SKW1561	Sewer (SMFH1-SMFH2, SMFH3-SMFH7)	220	0	24/02/14	02/10/14	25/07/13	01/03/14	-215d	SKW1551	SKW1571						
SKW1571	Roadwork & Drainage Channel (SKW)	220	0	02/10/14	10/05/15	02/03/14	07/10/14	-215d	SKW1561	KD0090						
<b>SKW STW - E&amp;M Works</b>																
E&M3170	Install Membrane Modules in MBR Tank No. 1 to 2	100	0	18/12/13	28/03/14	07/01/14	16/04/14	19d	E&M3010, SKW1451	E&M3311						
E&M3190	Install Grit Removal Equipment	60	0	16/02/14	17/04/14	21/09/13	19/11/13	-149d	E&M3030, E&M3210, SKW1451	E&M3250, E&M3320						
E&M3210	Install Fine Screens	60	0	18/12/13	16/02/14	24/05/13	22/07/13	-209d	E&M3060, SKW1451	E&M3190, E&M3220, E&M3250, E&M3260, E&M3320	Install Fine Screens					
E&M3220	Install Pumps	75	0	16/02/14	02/05/14	23/07/13	05/10/13	-209d	E&M3070, E&M3210	E&M3230, E&M3250, E&M3260,						
E&M3230	Install Submersible Mixers	45	0	02/05/14	16/06/14	06/10/13	19/11/13	-209d	E&M3080, E&M3220	E&M3250, E&M3260, E&M3311,						
E&M3240	Install Sludge Dewatering Equipment	74	0	01/02/14	15/04/14	12/01/14	26/03/14	-20d	E&M3090, SKW1401, SKW1421	E&M3320						
E&M3250	Install Valves, Pipes & Fittings	75	0	16/06/14	30/08/14	20/11/13	02/02/14	-209d	E&M3100, E&M3190, E&M3210, E&M3220, E&M3230	E&M3270, E&M3291, E&M3300, E&M3310						
E&M3260	Install Penstocks	135	10	05/03/14 A	16/10/14	05/03/14 A	16/04/14	-182d	E&M3110, E&M3210, E&M3220,	E&M3311						
E&M3261	Install SAT of MCC & LVSB	174	0	30/05/14	20/11/14	04/10/13	26/03/14	-239d	E&M3140, SKW1301, SKW1411	E&M3311, E&M3320						
E&M3270	Install instruments	60	0	30/08/14	29/10/14	16/02/14	16/04/14	-196d	E&M3130, E&M3250	E&M3311						
E&M3291	Install BS Equipment	180	0	01/07/14	28/12/14	05/12/13	02/06/14	-209d	E&M3150, E&M3250, SKW1301, SKW1411, SKW1451	E&M3331, E&M3359						

Start date	05/05/10
Finish date	20/10/17
Data date	30/11/13
Run date	04/03/14
Page number	10A
c Primavera Systems, Inc.	

	Early bar
	Progress bar
	Critical bar
	Summary bar
	Progress point
	Critical point
	Summary point
	Start milestone point
	Finish milestone point

**Leader Civil Engineering Corp. Ltd.**  
**Contract No. DC/2009/13**  
**Construction of Sewage Treatment Works at YSW & SKW**  
**3-month Rolling Programme (Feb 2014 - April 201)**

Date	Revision	Checked	Approved
31/01/14	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	OCT	2013 NOV	DEC	JAN	2014 FEB	MAR
E&M3300	Install FS Equipment	161	0	06/07/14	14/12/14	24/12/13	02/06/14	-195d	E&M3160, E&M3250, SKW1451	E&M3331, E&M3359						
E&M3310	Hydraulic Tests of Pipeworks	90	0	30/08/14	28/11/14	06/03/14	03/06/14	-178d	E&M3250	E&M3359						
E&M3311	Cabling Works	47	0	20/11/14	06/01/15	17/04/14	02/06/14	-218d	E&M3170, E&M3230, E&M3260, E&M3261, E&M3270, SKW1301,	E&M3331, E&M3359						
E&M3320	Cabling Works for Dewatering Equipment	47	0	20/11/14	06/01/15	27/03/14	12/05/14	-239d	E&M3190, E&M3210, E&M3220, E&M3230, E&M3240, E&M3261	E&M3321						
E&M3321	Insulation Tests of Cables and Cable Termination	21	0	06/01/15	27/01/15	13/05/14	02/06/14	-239d	E&M3320	E&M3331						
E&M3331	Energization	1	0	27/01/15	28/01/15	03/06/14	03/06/14	-239d	E&M3291, E&M3300, E&M3311,	E&M3359						
E&M3359	Functional and Performance Tests of Equipment	35	0	28/01/15	04/03/15	04/06/14	08/07/14	-239d	E&M3291, E&M3300, E&M3310, E&M3311, E&M3331, SKW1241,	E&M3360						
E&M3360	T&C Period	91	0	04/03/15	03/06/15	09/07/14	07/10/14	-239d	E&M0340, E&M3359, SKW0722, SKW15112	E&M3370, KD0090						
E&M3370	Trial Operation Period	456	0	03/06/15	02/11/16	10/02/16	20/10/17	252d	E&M3360							
<b>Rising Main</b>																
SKW1481	Subm, Approval & Delivery of DI pipes	120	100	17/05/10 A	13/09/10 A	17/05/10 A	13/09/10 A		KD0020	SKW1501						
SKW1501	LCS (ChB0+00 - ChB1+20)	300	100	14/09/10 A	10/07/11 A	14/09/10 A	10/07/11 A		PRE0100, SKW1481	SKW1521						
SKW1521	Twin DN150 DI Rising Main (ChB0+00 - ChA4+55)	250	90	11/07/11 A	24/12/13	11/07/11 A	07/10/14	287d	SKW1501	KD0090						
<b>Section W8 - Landscape Softworks in All Portions</b>																
SKW1591	Tree Survey	21	100	17/05/10 A	06/06/10 A	17/05/10 A	06/06/10 A		KD0020	SKW1621						
SKW1611	Preservation & Protection of Trees	1053	99	17/05/10 A	10/12/13	17/05/10 A	03/04/13	-251d	KD0020	KD0100, SKW1631						
SKW1621	Transplantation at SKW	90	100	07/06/10 A	04/09/10 A	07/06/10 A	04/09/10 A		SKW1591	KD0100						
<b>Section W9 - Establishment Works in All Portions</b>																
SKW1631	Section W9 - Establishment Works	365	0	10/12/13	10/12/14	04/04/13	03/04/14	-251d	SKW1611	KD0110						

Start date	05/05/10		Early bar
Finish date	20/10/17		Progress bar
Data date	30/11/13		Critical bar
Run date	04/03/14		Summary bar
Page number	11A		Progress point
			Critical point
			Summary point
			Start milestone point
			Finish milestone point


**Leader Civil Engineering Corp. Ltd.**  
**Contract No. DC/2009/13**  
**Construction of Sewage Treatment Works at YSW & SKW**  
**3-month Rolling Programme (Feb 2014 - April 2015)**


Date	Revision	Checked	Approved
31/01/14	Revision 0	RH	VC





## **Appendix D**

### **Location of Monitoring Stations (Air Quality / Construction Noise / Water Quality)**

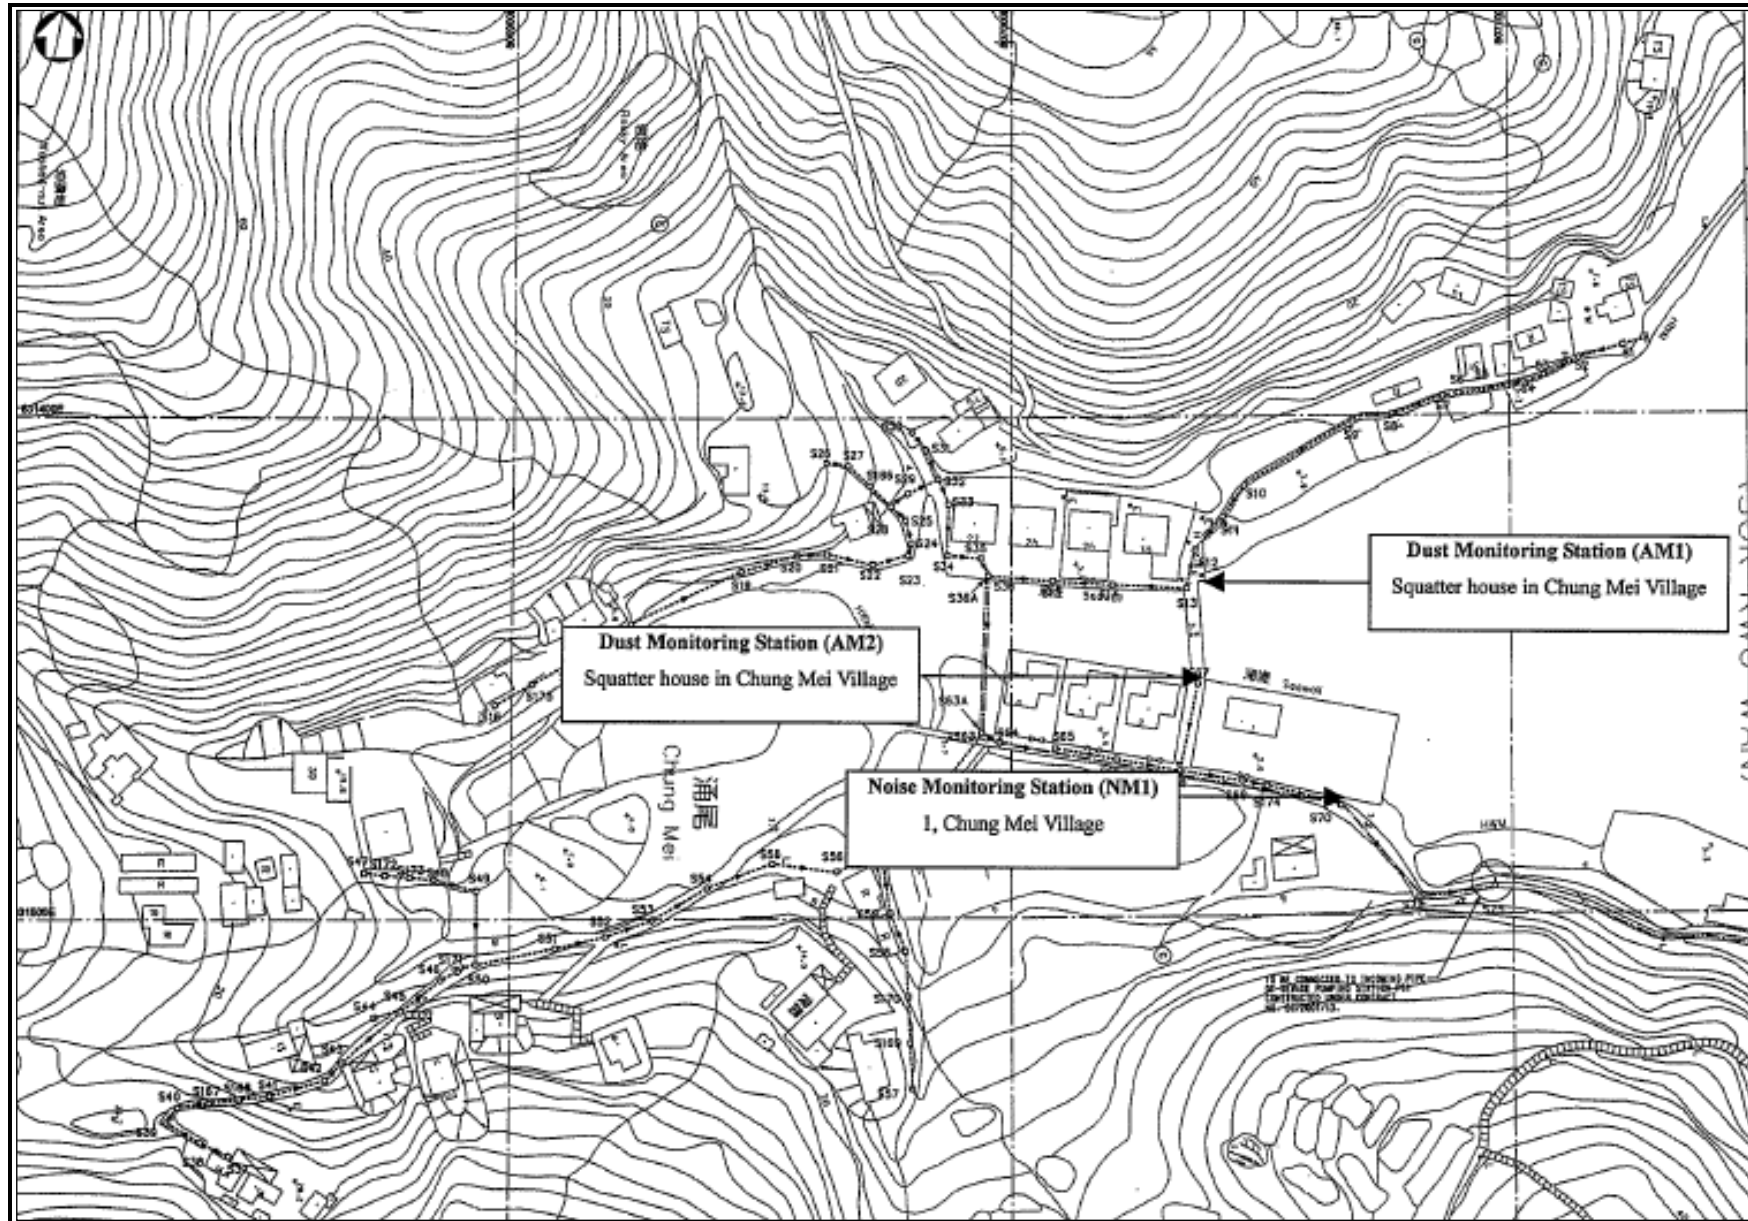

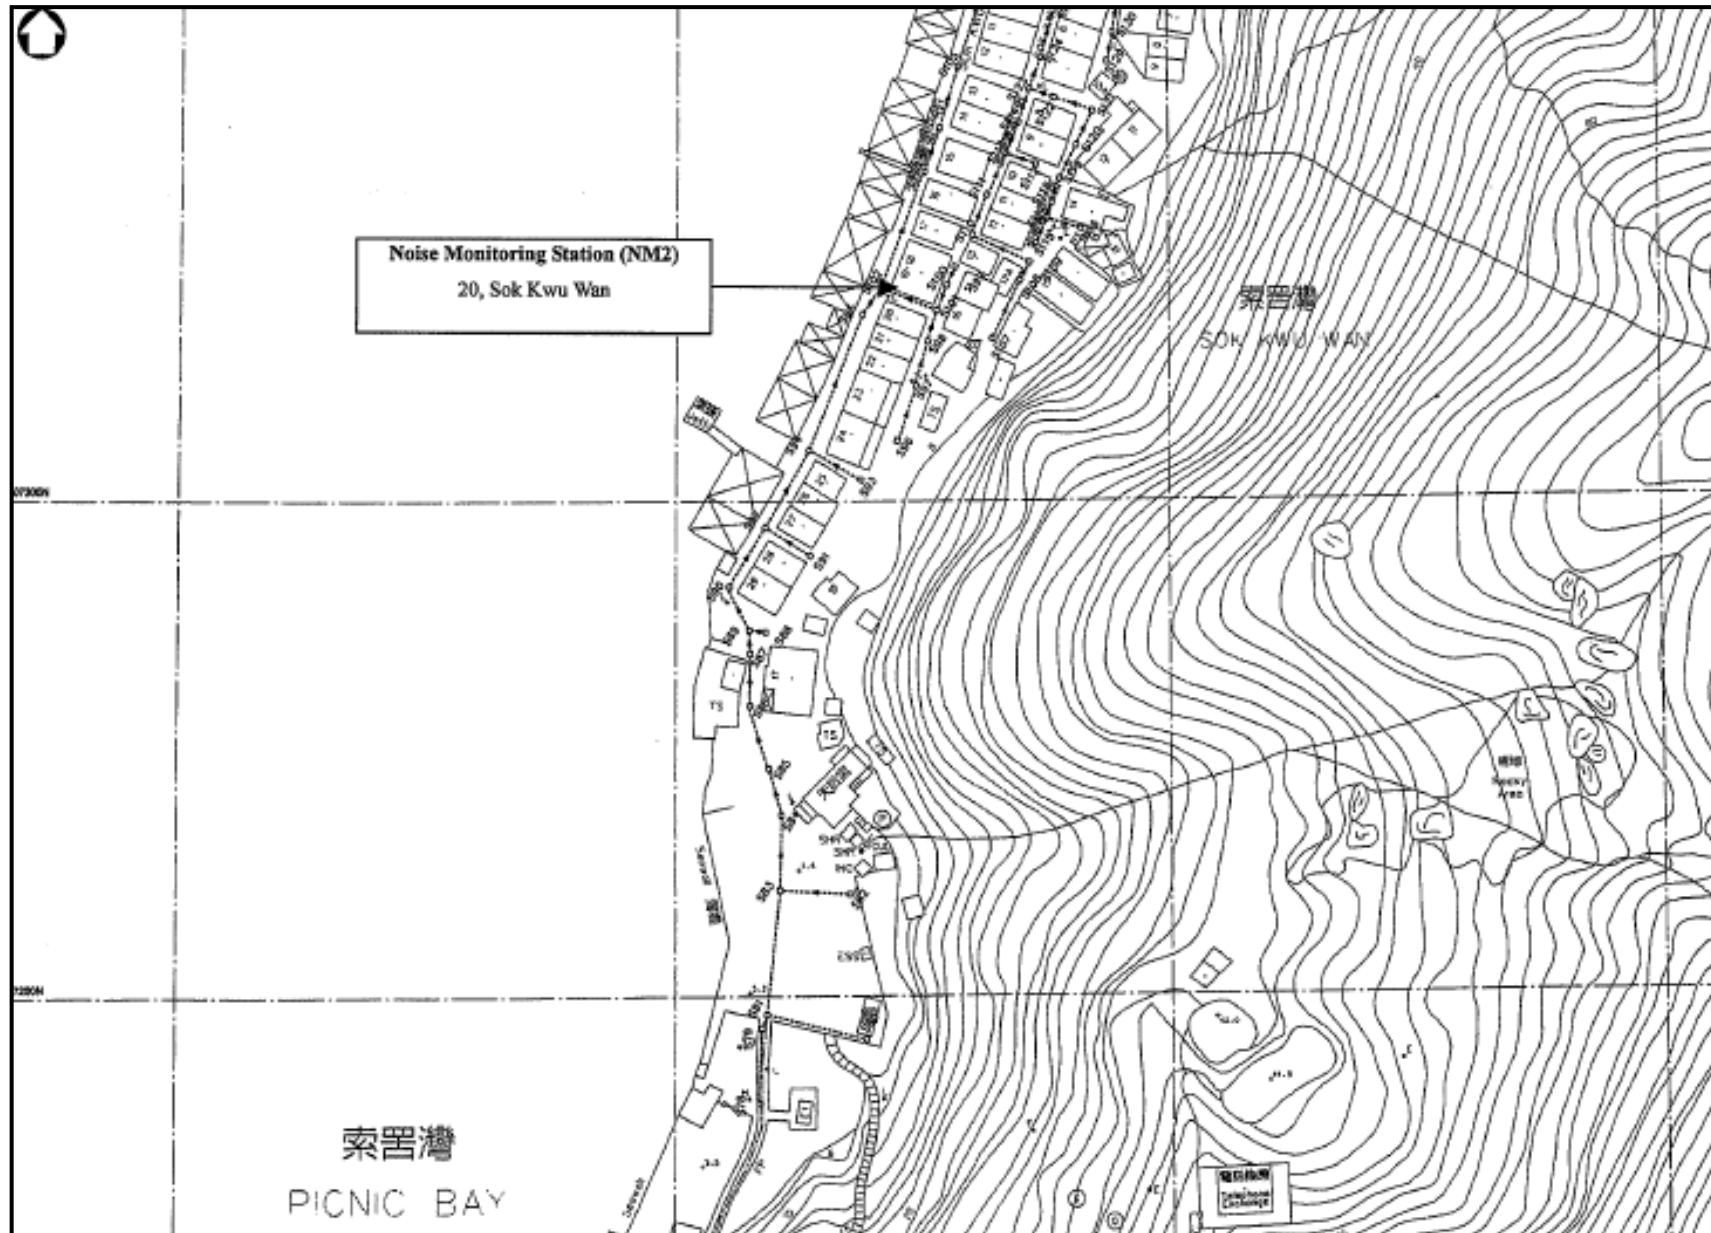

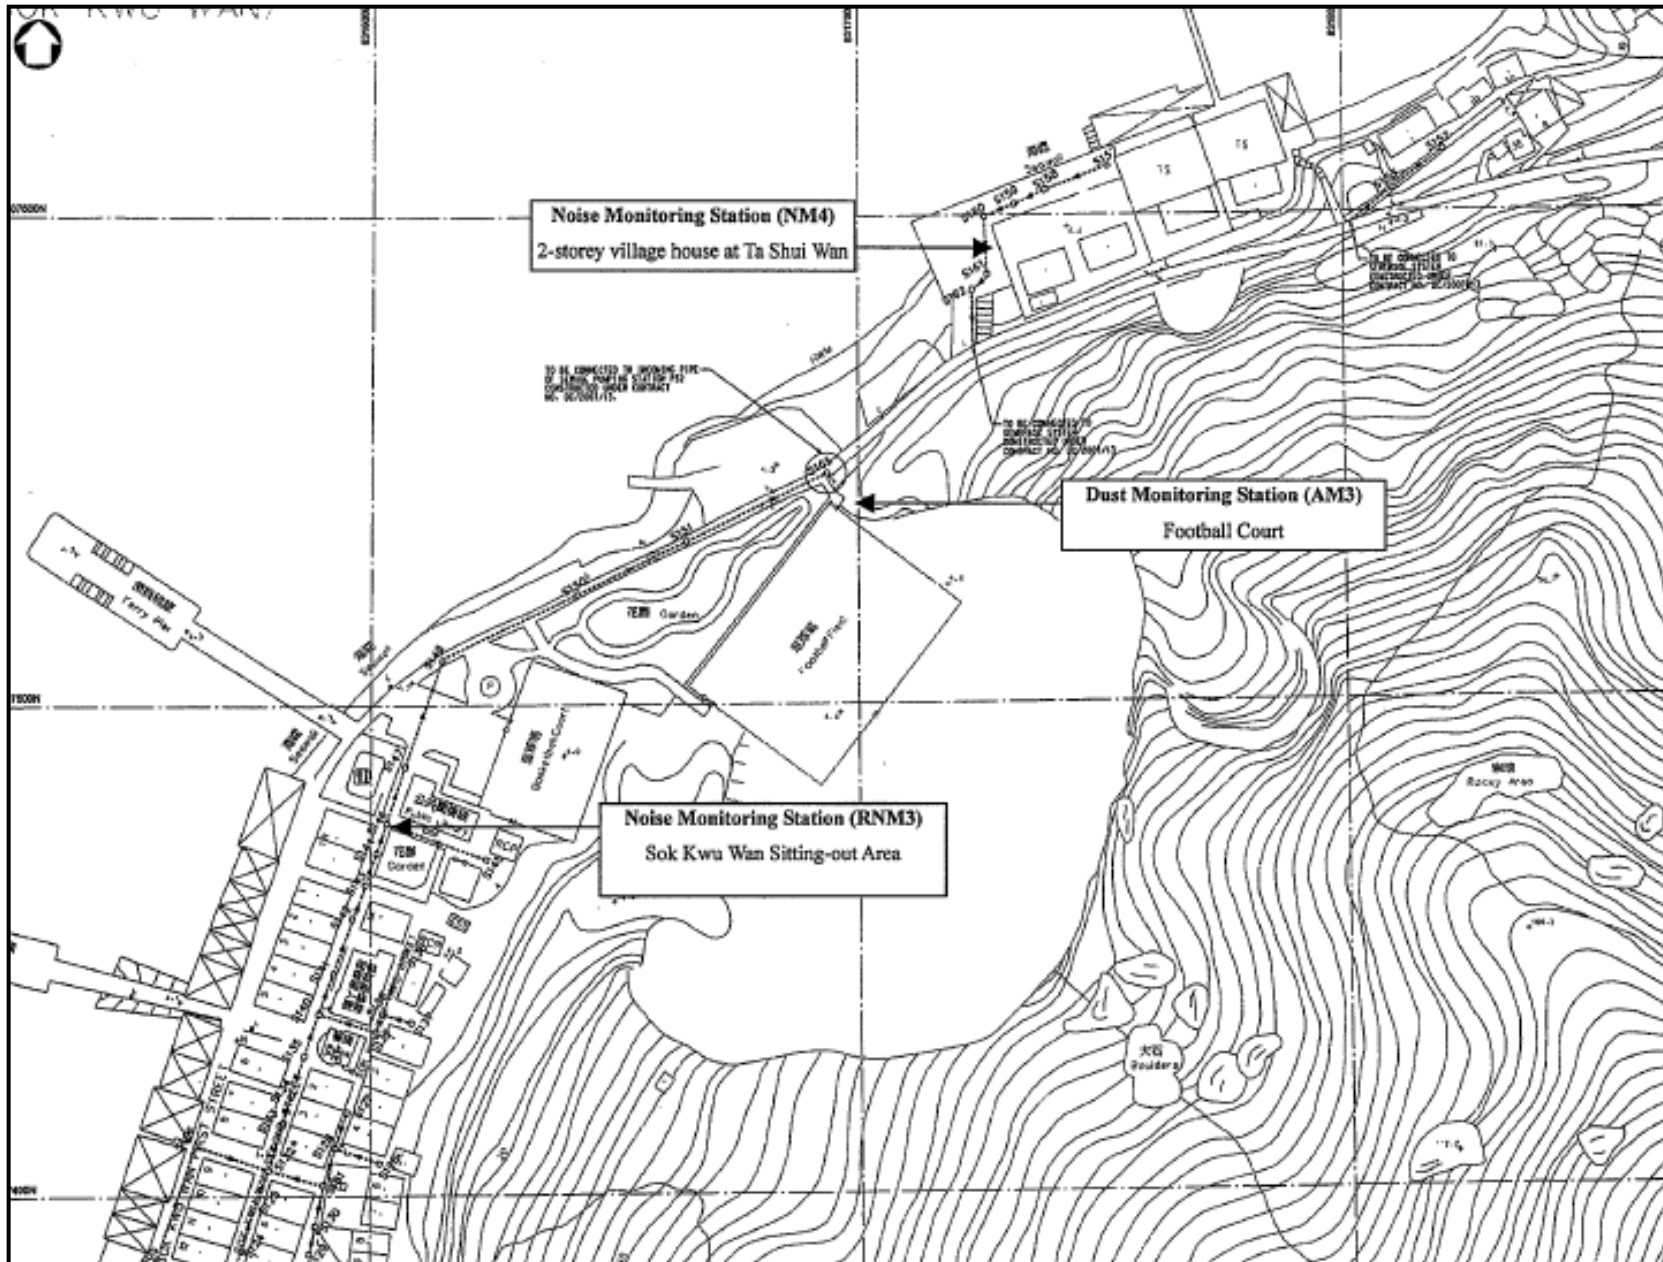

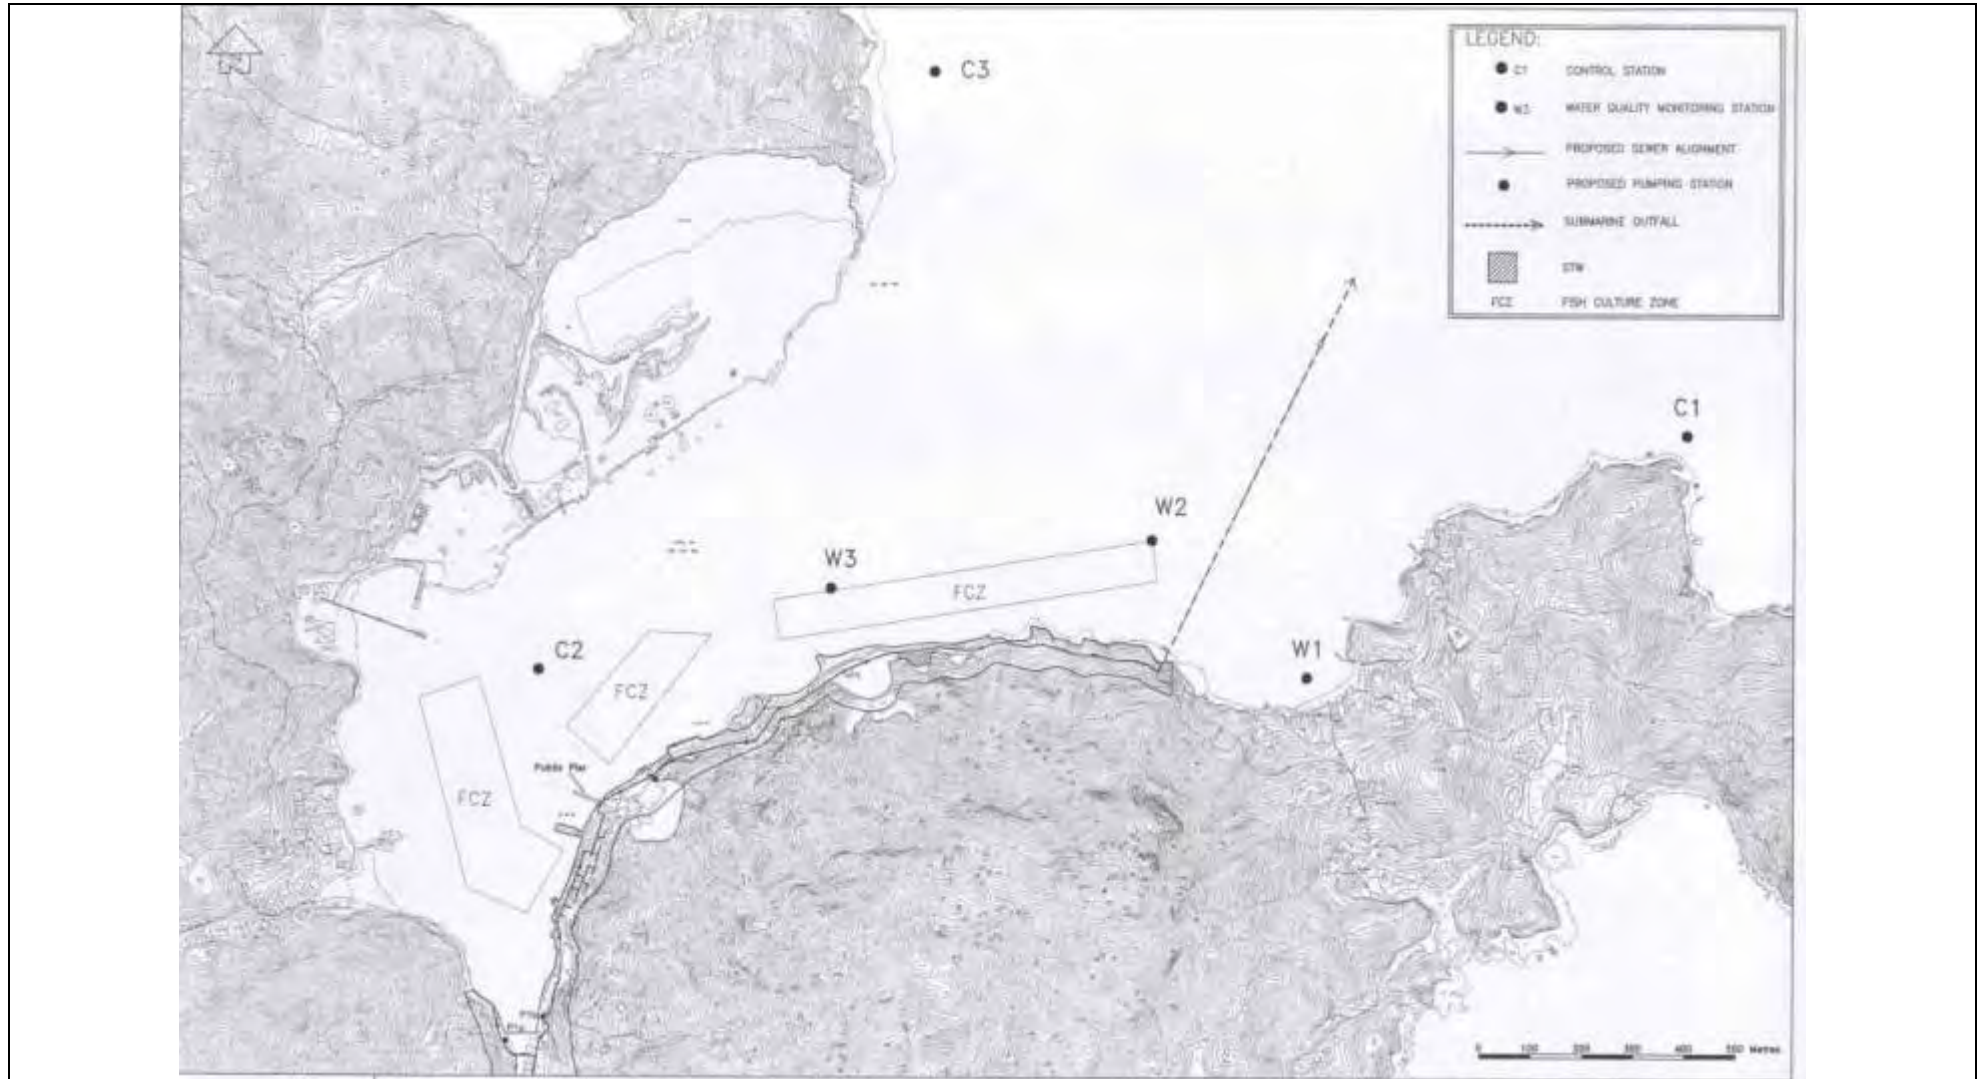

**Appendix E**

**Monitoring Equipments Calibration Certificate**




# CERTIFICATE OF CALIBRATION AND TESTING

TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA  
Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com

Environment Condition			Model	AM510
Temperature	73.2 (22.9)	°F (°C)		
Relative Humidity	44	%RH	Serial Number	11008018
Barometric Pressure	28.94 (980.0)	inHg (hPa)		

<input checked="" type="checkbox"/> As Left	<input checked="" type="checkbox"/> In Tolerance
<input type="checkbox"/> As Found	<input type="checkbox"/> Out of Tolerance

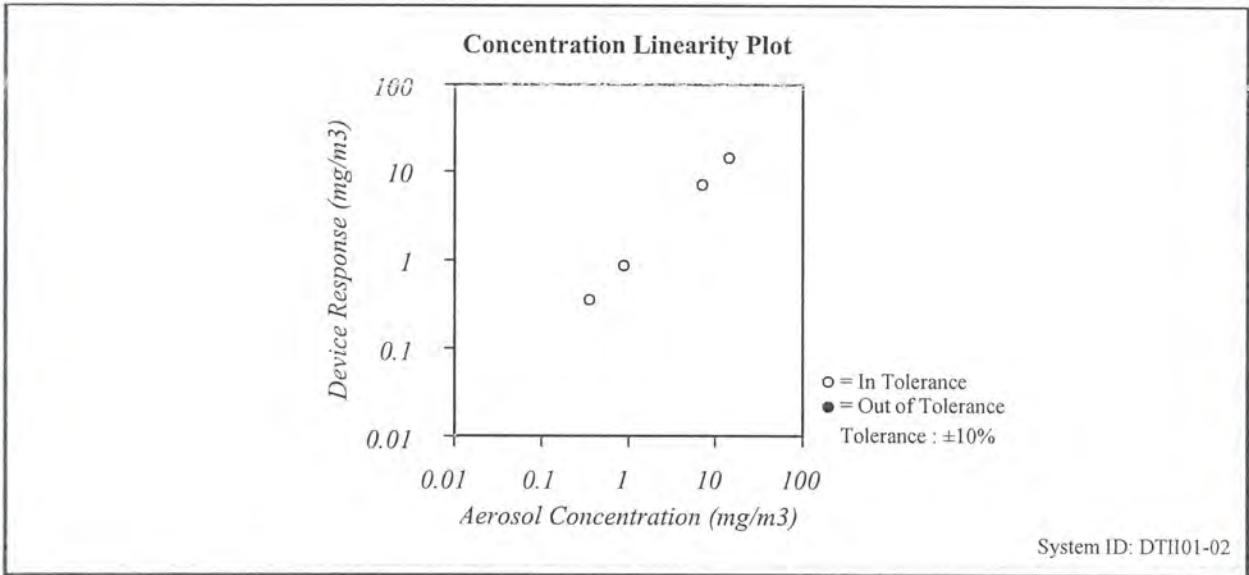

TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass of standard ISO 12103-1, A1 test dust (Arizona dust). Our calibration ratio is greater than 1.2:1

Measurement Variable	System ID	Last Cal.	Cal. Due	Measurement Variable	System ID	Last Cal.	Cal. Due
Barometric Pressure	E003733	03-12-13	03-12-14	Temperature	E002873	11-08-12	11-08-13
Humidity	E002873	11-08-12	11-08-13	DC Voltage	E003314	01-02-13	01-02-14
DC Voltage	E003315	01-02-13	01-02-14	Photometer	E003319	02-19-13	08-19-13
Microbalance	M001324	01-04-13	01-04-15	Pressure	E003511	11-07-12	11-07-13
Flowmeter	E002006	03-05-13	03-05-14				

*Amanda Shao*  
\_\_\_\_\_  
Calibrated

Final Function  
Check

July 25, 2013  
\_\_\_\_\_  
Date




# CERTIFICATE OF CALIBRATION AND TESTING

TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA  
 Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com

Environment Condition			Model	AM510
Temperature	69.1 (20.6)	°F (°C)		
Relative Humidity	46	%RH		
Barometric Pressure	29.07 (984.4)	inHg (hPa)		
			Serial Number	11008017

<input checked="" type="checkbox"/> As Left	<input checked="" type="checkbox"/> In Tolerance
<input type="checkbox"/> As Found	<input type="checkbox"/> Out of Tolerance

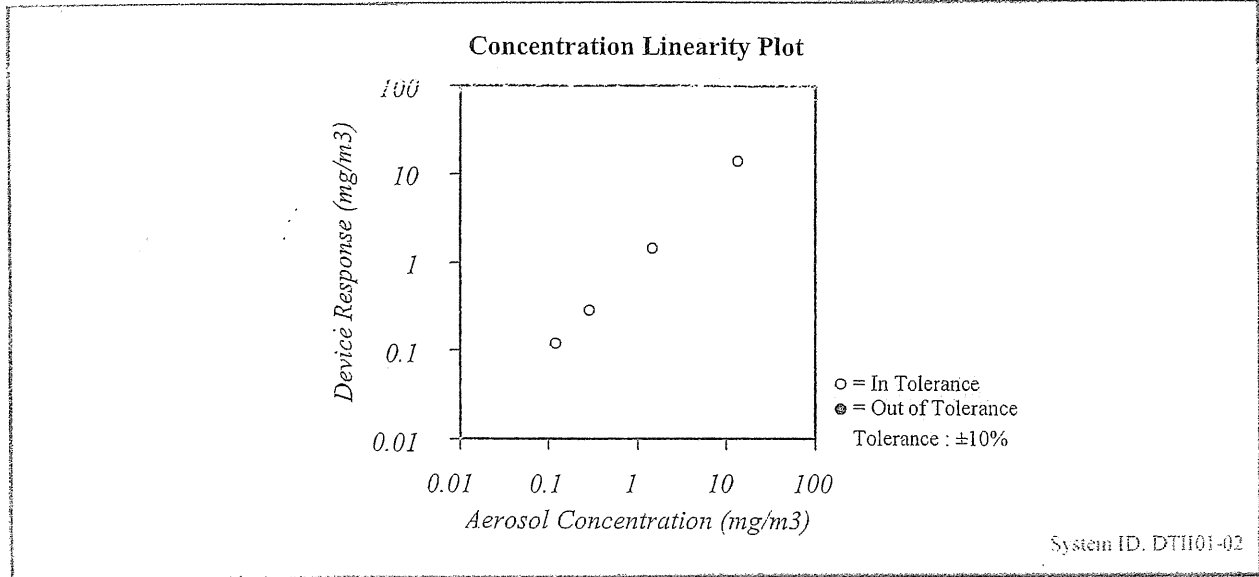

*TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass of standard ISO 12103-1. All test dust (Arizona dust). Our calibration ratio is greater than 1.2:1.*

Measurement Variable	System ID	Last Cal	Cal Due	Measurement Variable	System ID	Last Cal	Cal Due
Barometric Pressure	E005733	03-12-13	03-12-14	Temperature	E002875	11-08-12	11-08-13
Humidity	E002873	11-08-12	11-08-13	DC Voltage	E003314	01-02-13	01-02-14
DC Voltage	E003315	01-02-13	01-02-14	Photometer	E003319	02-19-13	03-19-13
Microbalance	M001324	01-04-13	01-04-15	Pressure	E003511	11-07-12	11-07-13
Flowmeter	E002006	03-05-13	03-05-14				

Amanda MAD  
 Calibrated

Final Function  
 Check

June 18, 2013  
 Date





# CERTIFICATE OF CALIBRATION AND TESTING


TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA  
Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com

Environment Condition			Model	8520
Temperature	74.7 (23.7)	°F (°C)	Serial Number	21060
Relative Humidity	27	%RH		
Barometric Pressure	28.97 (981.0)	inHg (hPa)		

As Left  
 As Found

In Tolerance  
 Out of Tolerance

### Concentration Linearity Plot

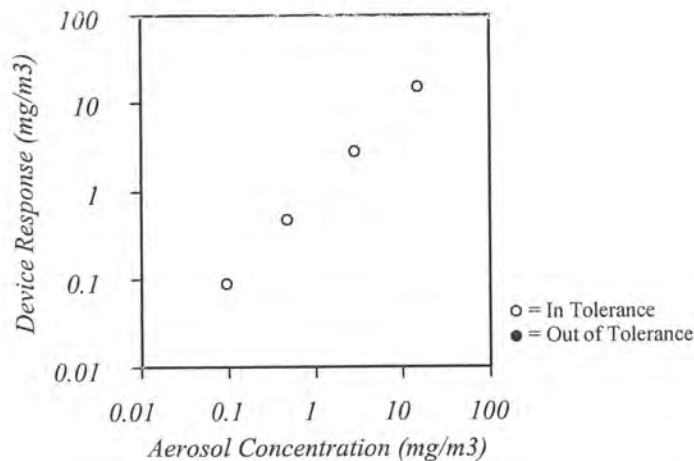

System ID: DT1101-02

### Zero Stability Results

Average: <i>0.00</i> :mg/m <sup>3</sup>	Minimum: <i>0.00</i> :mg/m <sup>3</sup>	Maximum: <i>0.00</i> :mg/m <sup>3</sup>	Time: <i>2.07</i> :hrs.
--	--	--	----------------------------

TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass of standard ISO 12103-1, A1 test dust (Arizona dust). Our calibration ratio is greater than 1.2:1

Measurement Variable	System ID	Last Cal.	Cal. Due	Measurement Variable	System ID	Last Cal.	Cal. Due
Barometric Pressure	E003733	03-12-13	03-12-14	Temperature	E002873	11-08-12	11-08-13
Humidity	E002873	11-08-12	11-08-13	DC Voltage	E003314	01-02-13	01-02-14
DC Voltage	E003315	01-02-13	01-02-14	Photometer	E003319	08-14-13	02-14-14
Microbalance	M001324	01-04-13	01-04-15	Pressure	E003511	11-07-12	11-07-13
Flowmeter	E002006	03-05-13	03-05-14				

*[Signature]*  
Calibrated

Final Function  
Check

October 22, 2013

Date



# CERTIFICATE OF CALIBRATION AND TESTING

TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA  
 Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com

Environment Condition			Model	8520
Temperature	74.8 (23.8)	°F (°C)	Serial Number	23080
Relative Humidity	27	%RH		
Barometric Pressure	28.96 (980.7)	inHg (hPa)		


 As Left

 In Tolerance

 As Found

 Out of Tolerance

### Concentration Linearity Plot

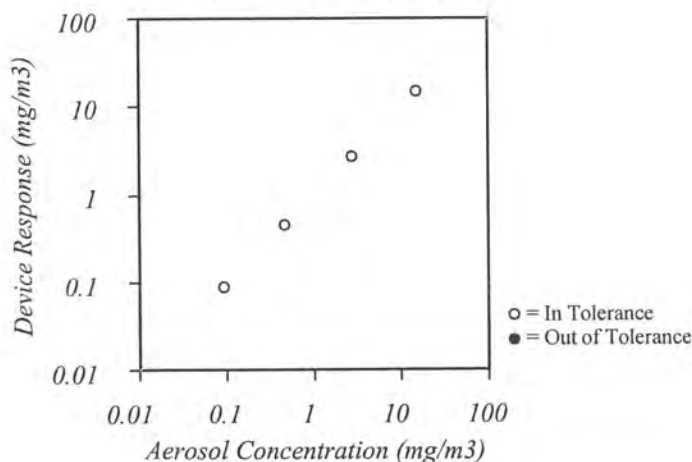

System ID: DTII01-02

### Zero Stability Results

Average:	Minimum:	Maximum:	Time:
0.000 :mg/m <sup>3</sup>	0.000 :mg/m <sup>3</sup>	0.001 :mg/m <sup>3</sup>	17:00 :hrs.

TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass of standard ISO 12103-1, A1 test dust (Arizona dust). Our calibration ratio is greater than 1.2:1

Measurement Variable	System ID	Last Cal.	Cal. Due	Measurement Variable	System ID	Last Cal.	Cal. Due
Barometric Pressure	E003733	03-12-13	03-12-14	Temperature	E002873	11-08-12	11-08-13
Humidity	E002873	11-08-12	11-08-13	DC Voltage	E003314	01-02-13	01-02-14
DC Voltage	E003315	01-02-13	01-02-14	Photometer	E003319	08-14-13	02-14-14
Microbalance	M001324	01-04-13	01-04-15	Pressure	E003511	11-07-12	11-07-13
Flowmeter	E002006	03-05-13	03-05-14				

*Tom Jay*  
 \_\_\_\_\_  
 Calibrated

 Final Function Check

October 22, 2013

Date

TSI P/N 2300157




# CERTIFICATE OF CALIBRATION AND TESTING

TSI Instruments Ltd, Stirling Road, Cressex Business Park  
High Wycombe Bucks HP12 3ST England  
Tel: (Int +44) (UK 0) 1494 459200 Fax: (Int +44) (UK 0) 1494 459700 <http://www.tsiinc.co.uk>

Environment Condition			Model	8520
Temperature	23.5	°C	Serial Number	23079
Relative Humidity	41.92	%RH		
Barometric Pressure	996.6	hPa		

<input checked="" type="checkbox"/> As Left	<input checked="" type="checkbox"/> In Tolerance
<input type="checkbox"/> As Found	<input type="checkbox"/> Out of Tolerance

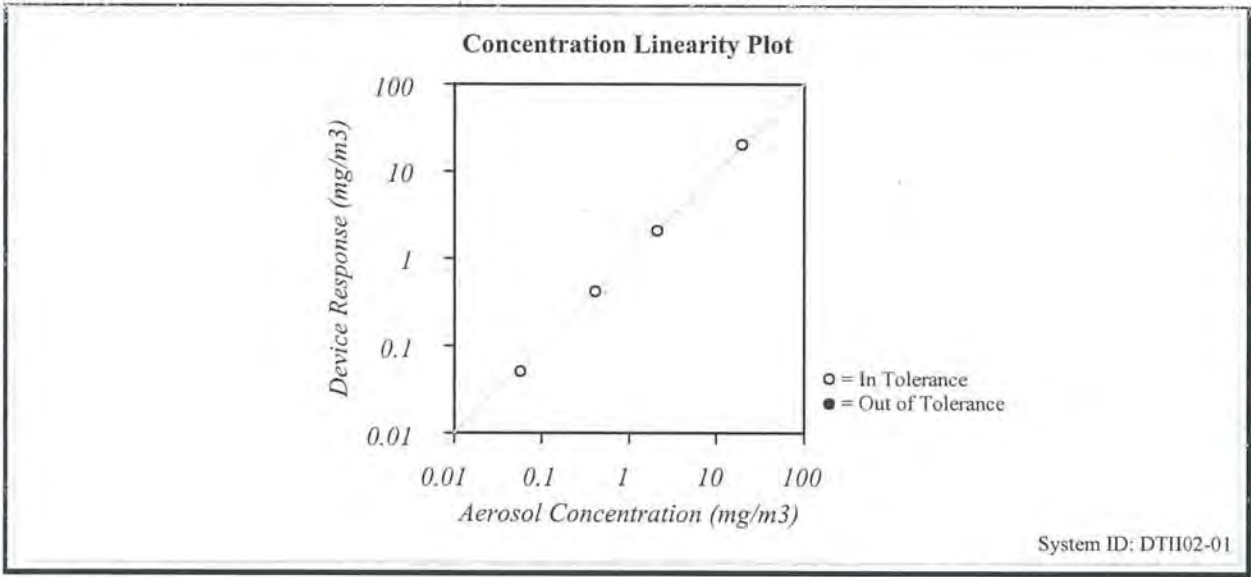

Zero Stability Results			
Average:	Minimum:	Maximum:	Time:
0.000 :mg/m <sup>3</sup>	0.000 :mg/m <sup>3</sup>	0.001 :mg/m <sup>3</sup>	4.00 :hrs.

*TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass of standard ISO 12103-1, A1 test dust (Arizona dust). Our calibration ratio is greater than 1.2:1*

Measurement Variable	System ID	Last Cal.	Cal. Due	Measurement Variable	System ID	Last Cal.	Cal. Due
Barometric Pressure	E006013	18-03-13	18-03-14	Temperature	E006014	18-03-13	18-03-14
Humidity	E006014	18-03-13	18-03-14	Photometer	E003336	06-03-13	06-09-13
Microbalance	UK 23403008	07-01-13	07-01-14	Flow and Temperature	E006128	29-01-13	29-01-14
Pressure	E006013	18-03-13	18-03-14	DC Voltage	E003323	19-10-12	19-10-13

 _____ Calibrated	<input checked="" type="checkbox"/> Final Function Check	17 June, 2013 _____ Date
-------------------------	--	--------------------------------

**CALIBRATION CERTIFICATE**

Date: June 20, 2013

Equipment Name	:	Laser Dust Monitor, Model LD-3B
Code No.	:	080000-42
Quantity	:	1 unit
Serial No.	:	366407
Sensitivity	:	0.001 mg/m <sup>3</sup>
Sensitivity Adjustment	:	563 CPM
Scale Setting	:	June 17, 2013

We hereby certify that the avobe mentioned instrmnt has been calibrated satisfactory.

Sincerely

**SIBATA SCIENTIFIC TECHNOLOGY LTD.**

Kentaro Togo

Overseas Sales Division

## CALIBRATION CERTIFICATE


Date: December 18, 2013

Equipment Name	:	Laser Dust Monitor, Model LD-3B
Code No.	:	080000-42
Quantity	:	1 unit
Serial No.	:	3Y6503
Sensitivity	:	0.001 mg/m <sup>3</sup>
Sensitivity Adjustment	:	663 CPM
Calibration Date	:	November 12, 2013

We hereby certify that the above mentioned instrument has been calibrated satisfactorily.

Sincerely

**SIBATA SCIENTIFIC TECHNOLOGY LTD.**



Kentaro Togo

Section Manager

Overseas Sales Division



SIBATA SCIENTIFIC TECHNOLOGY LTD.

1-1-62, Nakane, Soka, Saitama, 340-0005 Japan

TEL : 048-933-1582 FAX : 048-933-1591


**CALIBRATION CERTIFICATE**

Date: December 18, 2013

Equipment Name	:	Laser Dust Monitor, Model LD-3B
Code No.	:	080000-42
Quantity	:	1 unit
Serial No.	:	3Y6501
Sensitivity	:	0.001 mg/m <sup>3</sup>
Sensitivity Adjustment	:	695 CPM
Calibration Date	:	November 12, 2013

We hereby certify that the above mentioned instrument has been calibrated satisfactorily.

Sincerely

**SIBATA SCIENTIFIC TECHNOLOGY LTD.**  
Kentaro Togo

Section Manager

Overseas Sales Division

# Certificate of Calibration

## 校正證書

Certificate No. : C132980

證書編號

### ITEM TESTED / 送檢項目 ( Job No. / 序引編號 : IC13-0878 )

Description / 儀器名稱 : Integrating Sound Level Meter (EQ065)  
Manufacturer / 製造商 : Brüel & Kjær  
Model No. / 型號 : 2238  
Serial No. / 編號 : 2337676  
Supplied By / 委託者 : Action-United Environmental Services and Consulting  
Unit A, 20/F., Gold King Industrial Building,  
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

### TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$   
Line Voltage / 電壓 : ---

Relative Humidity / 相對濕度 :  $(55 \pm 20)\%$

### TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 18 May 2013


### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
All results are within manufacturer's specification.  
The results are detailed in the subsequent page(s).


The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By  
測試

:   
K C Lee

Certified By  
核證

:   
K M Wu

Date of Issue :  
簽發日期

20 May 2013

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C132980

證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration using laboratory acoustic calibrator was performed before the test from 6.1.1.2 to 6.4.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C130019
CL281	Multifunction Acoustic Calibrator	DC110233

- Test procedure : MA101N.

- Results :

### 6.1 Sound Pressure Level

#### 6.1.1 Reference Sound Pressure Level

##### 6.1.1.1 Before Self-calibration

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
50 - 130	L <sub>AFP</sub>	A	F	94.00	1	93.6

##### 6.1.1.2 After Self-calibration

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L <sub>AFP</sub>	A	F	94.00	1	94.0	± 0.7

### 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
50 - 130	L <sub>AFP</sub>	A	F	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.0

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。



# Certificate of Calibration

## 校正證書

Certificate No. : C132980

證書編號

### 6.2 Time Weighting

#### 6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L <sub>AFP</sub>	A	F	94.00	1	94.0	Ref.
	L <sub>ASP</sub>		S			94.0	± 0.1
	L <sub>AIP</sub>		I			94.0	± 0.1

#### 6.2.2 Tone Burst Signal (2 kHz)

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Burst Duration		
30 - 110	L <sub>AFP</sub>	A	F	106.0	Continuous	106.0	Ref.
	L <sub>AFMax</sub>				200 ms	105.0	-1.0 ± 1.0
	L <sub>ASP</sub>		S		Continuous	106.0	Ref.
	L <sub>ASMax</sub>				500 ms	102.0	-4.1 ± 1.0

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L <sub>AFP</sub>	A	F	94.00	31.5 Hz	54.9	-39.4 ± 1.5
					63 Hz	67.9	-26.2 ± 1.5
					125 Hz	77.9	-16.1 ± 1.0
					250 Hz	85.3	-8.6 ± 1.0
					500 Hz	90.7	-3.2 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	95.2	+1.2 ± 1.0
					4 kHz	95.0	+1.0 ± 1.0
					8 kHz	92.9	-1.1 (+1.5 ; -3.0)
					12.5 kHz	89.8	-4.3 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C132980  
證書編號

### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L <sub>CFP</sub>	C	F	94.00	31.5 Hz	91.2	-3.0 ± 1.5
					63 Hz	93.2	-0.8 ± 1.5
					125 Hz	93.8	-0.2 ± 1.0
					250 Hz	93.9	0.0 ± 1.0
					500 Hz	94.0	0.0 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	93.8	-0.2 ± 1.0
					4 kHz	93.2	-0.8 ± 1.0
					8 kHz	91.0	-3.0 (+1.5 ; -3.0)
					12.5 kHz	87.9	-6.2 (+3.0 ; -6.0)

### 6.4 Time Averaging

UUT Setting				Applied Value					UUT Reading (dB)	IEC 60804 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Integrating Time	Frequency (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)		
30 - 110	L <sub>Aeq</sub>	A	10 sec.	4	1	1/10	110.0	100	99.9	± 0.5
								90	89.9	± 0.5
								80	79.8	± 1.0
								70	69.5	± 1.0

Remarks : - UUT Microphone Model No. : 4188 & S/N : 2793313

- Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :

94 dB	31.5 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	12.5 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
Burst equivalent level		: ± 0.2 dB (Ref. 110 dB continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

#### Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。



# Certificate of Calibration 校正證書

Certificate No. : C132229  
證書編號

**ITEM TESTED / 送檢項目** ( Job No. / 序引編號 : IC13-0878 )

Description / 儀器名稱 : Precision Integrating Sound Level Meter (EQ012)  
Manufacturer / 製造商 : Rion  
Model No. / 型號 : NL-14  
Serial No. / 編號 : 10303225  
Supplied By / 委託者 : Action-United Environmental Services and Consulting  
Unit A, 20/F., Gold King Industrial Building,  
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

**TEST CONDITIONS / 測試條件**

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$       Relative Humidity / 相對濕度 :  $(55 \pm 20)\%$   
Line Voltage / 電壓 : ---

**TEST SPECIFICATIONS / 測試規範**

Calibration check

**DATE OF TEST / 測試日期** : 15 April 2013

**TEST RESULTS / 測試結果**

The results apply to the particular unit-under-test only.  
All results are within manufacturer's specification.  
The results are detailed in the subsequent page(s).


The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By  
測試

  
K C Lee

Certified By  
核證

  
K M Wu

Date of Issue  
簽發日期

16 April 2013

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C132229

證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C130019
CL281	Multifunction Acoustic Calibrator	DC110233

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
40 - 100	L <sub>p</sub>	A	Fast	94.00	1	93.8	± 0.7

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
60 - 120	L <sub>p</sub>	A	Fast	94.00	1	93.7 (Ref.)
				104.00		103.7
				114.00		113.8

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

# Certificate of Calibration

## 校正證書

Certificate No. : C132229

證書編號

### 6.2 Time Weighting

#### 6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
40 - 100	L <sub>p</sub>	A	Fast	94.00	1	93.8	Ref.
			Slow			93.8	± 0.1
			Imp			93.8	± 0.1

#### 6.2.2 Tone Burst Signal (2 kHz)

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mose	Frequency Weighting	Time Weighting	Level (dB)	Burst Duration		
50 - 110	L <sub>p</sub>	A	Fast	106.0	Continuous	106.0	Ref.
	L <sub>Amax</sub>				200 ms	105.2	-1.0 ± 1.0
	L <sub>p</sub>		Slow		Continuous	106.0	Ref.
	L <sub>Amax</sub>				500 ms	102.1	-4.1 ± 1.0

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
40 - 100	L <sub>p</sub>	A	Fast	94.00	31.5 Hz	54.4	-39.4 ± 1.5
					63 Hz	67.7	-26.2 ± 1.5
					125 Hz	77.8	-16.1 ± 1.0
					250 Hz	85.3	-8.6 ± 1.0
					500 Hz	90.6	-3.2 ± 1.0
					1 kHz	93.8	Ref.
					2 kHz	95.0	+1.2 ± 1.0
					4 kHz	94.7	+1.0 ± 1.0
					8 kHz	92.5	-1.1 (+1.5 ; -3.0)
12.5 kHz	89.3	-4.3 (+3.0 ; -6.0)					

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C132229  
證書編號

### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
40 - 100	L <sub>p</sub>	C	Fast	94.00	31.5 Hz	90.8	-3.0 ± 1.5
					63 Hz	93.0	-0.8 ± 1.5
					125 Hz	93.7	-0.2 ± 1.0
					250 Hz	93.9	0.0 ± 1.0
					500 Hz	93.9	0.0 ± 1.0
					1 kHz	93.9	Ref.
					2 kHz	93.7	-0.2 ± 1.0
					4 kHz	93.0	-0.8 ± 1.0
					8 kHz	90.7	-3.0 (+1.5 ; -3.0)
12.5 kHz	87.5	-6.2 (+3.0 ; -6.0)					

### 6.4 Time Averaging

UUT Setting				Applied Value					UUT Reading (dB)	IEC 60804 Type 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Frequency (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)		
50 - 110	L <sub>Aeq</sub>	A	10 sec.	4	1	1/10	110.0	100	99.8	± 0.5
								90	89.6	± 0.5
								80	79.3	± 1.0
								70	70.0	± 1.0
			60 sec.							
			5 min.							

Remarks : - UUT Microphone Model No. : UC-53A & S/N : 319944

- Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :

94 dB : 31.5 Hz - 125 Hz	: ± 0.35 dB
250 Hz - 500 Hz	: ± 0.30 dB
1 kHz	: ± 0.20 dB
2 kHz - 4 kHz	: ± 0.35 dB
8 kHz	: ± 0.45 dB
12.5 kHz	: ± 0.70 dB
104 dB : 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB : 1 kHz	: ± 0.10 dB (Ref. 94 dB)
Burst equivalent level	: ± 0.2 dB (Ref. 110 dB continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

#### Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。



# Certificate of Calibration 校正證書

Certificate No. : C132228  
證書編號

**ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC13-0878)**

Description / 儀器名稱 : Acoustical Calibrator (EQ081)  
Manufacturer / 製造商 : Brüel & Kjær  
Model No. / 型號 : 4231  
Serial No. / 編號 : 2326408  
Supplied By / 委託者 : Action-United Environmental Services and Consulting  
Unit A, 20/F., Gold King Industrial Building,  
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

**TEST CONDITIONS / 測試條件**

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$       Relative Humidity / 相對濕度 :  $(55 \pm 20)\%$   
Line Voltage / 電壓 : ---

**TEST SPECIFICATIONS / 測試規範**

Calibration check

**DATE OF TEST / 測試日期** : 15 April 2013


**TEST RESULTS / 測試結果**

The results apply to the particular unit-under-test only.  
All results are within manufacturer's specification.  
The results are detailed in the subsequent page(s).


The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By  
測試

:   
K C Lee

Certified By  
核證

:   
K M Wu

Date of Issue : 16 April 2013  
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準，局部複印本證書需先獲本實驗室書面批准。



# Certificate of Calibration

## 校正證書

Certificate No. : C132228  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C123541
CL281	Multifunction Acoustic Calibrator	DC110233
TST150A	Measuring Amplifier	C120886

- Test procedure : MA100N.

- Results :

### 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.0		

### 5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

### Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



## **Appendix F**

### **Event/Action Plan**

### Air Quality

EVENT	ACTION ET	IC(E)	ER	CONTRACTOR
<b>ACTION LEVEL</b>				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IC(E) and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method.	1. Notify Contractor.	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IC(E) and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IC(E) and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IC(E) and ER; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented.	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
<b>LIMIT LEVEL</b>				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
2. Exceedance for two or more consecutive samples	1. Notify IC(E), ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IC(E) and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IC(E), agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

### Construction Noise

EVENT	ACTION	IC(E)	ER	CONTRACTOR
	<b>ET</b>	<b>IC(E)</b>	<b>ER</b>	<b>CONTRACTOR</b>
Action Level	<ol style="list-style-type: none"> <li>1. Notify IC(E) and Contractor;</li> <li>2. Carry out investigation;</li> <li>3. Report the results of investigation to the IC(E), ER and Contractor;</li> <li>4. Discuss with the Contractor and formulate remedial measures;</li> <li>5. Increase monitoring frequency to check mitigation effectiveness</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the analysed results submitted by the ET;</li> <li>2. Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>4. Ensure remedial measures are properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to IC(E);</li> <li>2. Implement noise mitigation proposals.</li> </ol>
Limit Level	<ol style="list-style-type: none"> <li>1. Identify source;</li> <li>2. Inform IC(E), ER, EPD and Contractor;</li> <li>3. Repeat measurements to confirm findings;</li> <li>4. Increase monitoring frequency;</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>6. Inform IC(E), ER and EPD the causes and actions taken for the exceedances;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>4. Ensure remedial measures properly implemented;</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IC(E) within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Resubmit proposals if problem still not under control;</li> <li>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>

### Water Quality

EVENT	ACTION			
	ET	IC(E)	ER	CONTRACTOR
<b>ACTION LEVEL</b>				
1. Exceedance for one sampling day	<ol style="list-style-type: none"> <li>Repeat in-situ measurement on the next day of exceedance to confirm findings;</li> <li>Identify source(s) of impact;</li> <li>Inform ICE, Contractor, ER, EPD and AFCD; and</li> <li>Check monitoring data, all plant, equipment and Contractor's working methods.</li> </ol>	<ol style="list-style-type: none"> <li>Check monitoring data submitted by ET and Contractor's working methods</li> </ol>	<ol style="list-style-type: none"> <li>Confirm receipt of notification of non-compliance in writing; and</li> <li>Notify Contractor</li> </ol>	<ol style="list-style-type: none"> <li>Information the ER and confirm notification of the non-compliance in writing;</li> <li>Rectify unacceptable practice; and</li> <li>Amend working methods if appropriate</li> </ol>
2. Exceedance for two or more consecutive sampling days	<ol style="list-style-type: none"> <li>Same as the above;</li> <li>Inform ICE, Contractor, ER, EPD and AFCD;</li> <li>Discuss mitigation measures with IC(E), RE and Contractor;</li> <li>Ensure well implementation of mitigation measures; and</li> <li>Increase the monitoring frequency to daily until no exceedance of Action Level</li> </ol>	<ol style="list-style-type: none"> <li>Same as the above;</li> <li>Discuss with ET and Contractor on possible remedial actions;</li> <li>Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; and</li> <li>Supervise the implementation of mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>Discuss with IC(E) on the proposed mitigation measures;</li> <li>Ensure well implementation of mitigation measures; and</li> <li>Assess the effectiveness of the implemented mitigation measures</li> </ol>	<ol style="list-style-type: none"> <li>Same as the above;</li> <li>Check all plant and equipment and consider changes of working methods;</li> <li>Submit proposal of additional mitigation measures to ER within 3 working days of notification and discuss with ET, IC(E), and ER; and</li> <li>Implement the agreed mitigation measures</li> </ol>
<b>LIMIT LEVEL</b>				
1. Exceedance for one sampling day	<ol style="list-style-type: none"> <li>Repeat in-situ measurement on the next day of exceedance to confirm findings;</li> <li>Identify source(s) of impact;</li> <li>Inform ICE, Contractor, ER, EPD and AFCD;</li> <li>Check monitoring data, all plant, equipment and Contractor's working methods; and</li> <li>Discuss mitigation measures with IC(E), RE and Contractor</li> </ol>	<ol style="list-style-type: none"> <li>Check monitoring data submitted by ET and Contractor's working method</li> <li>Discuss with ER and Contractor on possible remedial actions; and</li> <li>Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly</li> </ol>	<ol style="list-style-type: none"> <li>Confirm receipt of notification failure in writing; and</li> <li>Discuss with IC(E), ET and Contractor on the proposed mitigation measures; and</li> <li>Request Contractor to review the working methods</li> </ol>	<ol style="list-style-type: none"> <li>Inform the ER and confirm notification of the failure in writing;</li> <li>Rectify unacceptable practice;</li> <li>Check all plant and equipment and consider changes of working methods; and</li> <li>Submit proposal of mitigation measures to ER within 3 working days of notification and discuss with ET and ER</li> </ol>
2. Exceedance for two or more consecutive sampling days	<ol style="list-style-type: none"> <li>Same as the above;</li> <li>Ensure mitigation measures are implemented; and</li> <li>Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days</li> </ol>	<ol style="list-style-type: none"> <li>Same as the above; and</li> <li>Supervise the Implementation of mitigation measures</li> </ol>	<ol style="list-style-type: none"> <li>Same as the above;</li> <li>Ensure well implementation of mitigation measures</li> <li>Make agreement on the mitigation measures to be implemented; and</li> <li>Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of limit level</li> </ol>	<ol style="list-style-type: none"> <li>Same as the above;</li> <li>Take immediate action to avoid further exceedance;</li> <li>Implement the agreed mitigation measures;</li> <li>Resubmit proposals of mitigation measures if problem still not under control; and</li> <li>As directed by the Engineer, to slow down or to stop all or part of the construction activities until to no exceedance of Limit Level.</li> </ol>

## **Appendix G**

### **Impact Monitoring Schedule**

### Impact Monitoring Schedule for the Reporting Period

Date		Air Quality		Noise	Water Quality
		1-hour TSP	24-hour TSP	Leq (30min)	
Sun	26-January-14				
Mon	27-January-14		✓		
Tue	28-January-14	✓		✓	✓
Wed	29-January-14				
Thu	30-January-14				✓
Fri	31-January-14				
Sat	1-February-14				
Sun	2- February -14				
Mon	3-February-14				
Tue	4-February-14		✓		✓
Wed	5-February-14	✓			
Thu	6-February-14			✓	✓
Fri	7-February-14				
Sat	8-February-14	✓			✓
Sun	9-February-14				
Mon	10-February-14		✓		✓
Tue	11-February-14				
Wed	12-February-14	✓		✓	✓
Thu	13-February-14				
Fri	14-February-14				
Sat	15-February-14		✓		✓
Sun	16-February-14				
Mon	17-February-14				
Tue	18-February-14	✓		✓	✓
Wed	19-February-14				
Thu	20-February-14				✓
Fri	21-February-14		✓		
Sat	22-February-14				✓
Sun	23-February-14				
Mon	24-February-14	✓		✓	✓
Tue	25-February-14				

✓	Monitoring Day
	Sunday or Public Holiday

### Impact Monitoring Schedule for next Reporting Period

Date		Air Quality		Noise	Water Quality
		1-hour TSP	24-hour TSP	Leq (30min)	
Wed	26-February-14				✓
Thu	27-February-14		✓		
Fri	28-February-14				
Sat	1-March-14	✓		✓	✓
Sun	2-March-14				
Mon	3-March-14				
Tue	4-March-14				✓
Wed	5-March-14		✓		
Thu	6-March-14	✓		✓	✓
Fri	7-March-14				
Sat	8-March-14				✓
Sun	9-March-14				
Mon	10-March-14				✓
Tue	11-March-14		✓		
Wed	12-March-14	✓		✓	✓
Thu	13-March-14				
Fri	14-March-14				
Sat	15-March-14				✓
Sun	16-March-14				
Mon	17-March-14		✓		
Tue	18-March-14	✓		✓	✓
Wed	19-March-14				
Thu	20-March-14				✓
Fri	21-March-14				
Sat	22-March-14		✓		✓
Sun	23-March-14				
Mon	24-March-14	✓		✓	✓
Tue	25-March-14				

✓	Monitoring Day
	Sunday or Public Holiday

## **Appendix H**

### **Monitoring Data Sheet**



## 24-hour TSP Monitoring Data Sheet

Air Quality Monitoring - 24-hour TSP Monitoring data sheet

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (oC)	STANDARD			INITIAL FILTER WEIGHT (g)	FINAL FILTER WEIGHT (g)	WEIGHT DUST COLLECTED (g)	DUST 24-hour TSP IN AIR (ug/m <sup>3</sup> )
		INITIAL	FINAL	ACTUAL (min)	MIN	MAX	AVG		AVG PRESS (hPa)	FLOW RATE (m3/min)	AIR VOLUME (std m3)				
<b>24-hour TSP Monitoring Results - AM1</b>															
27-Jan-14	26376	14541.83	14565.82	1439.40	34	39	36.5	15.4	1020.9	1.05	1516	2.7649	2.8533	0.0884	58
4-Feb-14	26398	14565.82	14589.81	1439.40	32	35	33.5	18.2	1013.3	0.97	1394	2.742	2.7731	0.0311	22
10-Feb-14	26402	14589.81	14613.8	1439.40	31	35	33	9.1	1019.1	0.97	1399	2.8204	2.9056	0.0852	61
15-Feb-14	26439	14613.8	14637.79	1439.40	30	37	33.5	11.8	1020.4	0.98	1412	2.7562	2.7975	0.0413	29
21-Feb-14	26452	14637.79	14661.78	1439.40	29	35	32	13.8	1024.5	0.94	1355	2.7064	2.7706	0.0642	47
<b>24-hour TSP Monitoring Results - AM2</b>															
27-Jan-14	26377	13044.92	13068.91	1439.40	31	37	34	15.4	1020.9	1.20	1725	2.7773	2.8943	0.1170	68
4-Feb-14	26397	13068.91	13092.9	1439.40	32	38	35	18.2	1013.3	1.22	1756	2.732	2.7932	0.0612	35
10-Feb-14	26404	13092.9	13116.89	1439.40	31	37	34	9.1	1019.1	1.21	1740	2.8711	2.9454	0.0743	43
15-Feb-14	26438	13116.89	13140.88	1439.40	29	35	32	11.8	1020.4	1.14	1647	2.7284	2.7873	0.0589	36
21-Feb-14	26453	13140.88	13164.87	1439.40	30	34	32	13.8	1024.5	1.14	1645	2.7345	2.7878	0.0533	32
<b>24-hour TSP Monitoring Results - AM3</b>															
27-Jan-14	26378	8514.86	8538.85	1439.4	42	45	43.5	15.4	1020.9	1.50	2163	2.7325	2.975	0.2425	112
4-Feb-14	26399	8538.85	8562.84	1439.4	42	46	44	18.2	1013.3	1.51	2168	2.746	2.8126	0.0666	31
10-Feb-14	26400	8562.84	8586.83	1439.4	40	43	41.5	9.1	1019.1	1.45	2093	2.7451	2.832	0.0869	42
15-Feb-14	26294	8586.83	8610.82	1439.4	41	44	42.5	11.8	1020.4	1.48	2130	2.7461	2.9017	0.1556	73
21-Feb-14	26455	8610.82	8634.81	1439.4	39	42	40.5	13.8	1024.5	1.42	2038	2.6789	2.7422	0.0633	31

## **Marine Water Quality Monitoring Data Sheet**

Contract No. DC/2009/13



**Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan**

**Sok Kwu Wan**

Date 28-Jan-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/1/28 10:52	W1	ME	832994	807728	2.7	1.350	17	8.93	114.5	1.6	32.47	8.14	3.1
						1.350	17	8.93	114.7	1.7	32.47	8.14	
2014/1/28 10:39	W2	ME	832692	807964	12.6	1.000	16.9	8.86	106.4	1.9	32.47	8.13	2.7
						1.000	16.9	8.88	108.2	2	32.48	8.13	
						6.300	16.7	8.89	109.7	2.1	32.49	8.12	3.5
						6.300	16.7	8.92	110.2	1.7	32.49	8.13	
						11.600	16.6	8.85	107.8	1.5	32.48	8.11	3.8
2014/1/28 10:17	W3	ME	832068	807916	11.8	11.600	16.6	8.87	108.3	2.2	32.48	8.11	
						1.000	17.3	8.85	106	2.4	32.49	8.1	3.8
						1.000	17.3	8.85	106.1	2	32.49	8.1	
						5.900	17.1	8.86	107.3	1.4	32.49	8.1	3.8
						5.900	17.1	8.86	107.5	1.9	32.49	8.1	
2014/1/28 11:01	C1	ME	833693	808198	15.9	10.800	16.7	8.86	107	2.2	32.49	8.11	4.3
						10.800	16.7	8.86	107.3	2.3	32.49	8.11	
						1.000	17	8.94	115.5	1.1	32.47	8.15	2.2
						1.000	17	8.94	115.5	1.2	32.47	8.15	
						7.950	16.7	8.91	112.1	1.5	32.48	8.13	3.5
2014/1/28 9:59	C2	ME	831455	807769	10.4	7.950	16.7	8.91	112.3	1.4	32.48	8.13	
						14.900	16.5	8.75	104.7	1.8	32.49	7.94	5.8
						14.900	16.5	8.75	104.8	1.9	32.49	7.94	
						1.000	17.4	9.11	109.3	2.4	32.47	8.07	3.9
						1.000	17.1	9.04	107.6	3.1	32.49	8.09	
2014/1/28 11:22	C3	ME	832229	808846	16.2	5.200	17.1	8.87	107.7	2.8	32.48	8.09	5.1
						5.200	17.1	8.87	107.5	2.1	32.49	8.1	
						9.400	16.8	8.82	109	2.6	32.49	8.1	4.2
						9.400	16.7	9.04	108	2.4	32.49	8.1	
						1.000	17	8.9	113.3	2.2	32.47	8.14	3.6
2014/1/28 15:55	W1	MF	832953	807719	2.8	1.000	17	8.9	113.4	3.1	32.46	8.14	
						8.100	16.6	8.9	113.7	2.7	32.47	8.13	4.4
						8.100	16.6	8.9	113.8	3.2	32.46	8.13	
						15.200	16.5	8.84	106.7	1.9	32.49	8.09	3.8
						15.200	16.5	8.84	106.5	2.3	32.49	8.09	
2014/1/28 15:55	W1	MF	832953	807719	2.8	1.400	16.6	8.87	105.1	1.7	32.48	8.12	3.8
						1.400	16.6	8.86	105.5	1.3	32.48	8.12	
2014/1/28 15:42	W2	MF	832668	807987	12.9	1.000	16.7	8.89	109.6	1.8	32.47	8.15	3.5
						1.000	16.7	8.89	109.9	1.9	32.47	8.14	
						6.450	16.5	8.86	104.1	2.1	32.52	8.09	3.7
						6.450	16.5	8.85	103.5	2.2	32.53	8.09	
						11.900	16.6	8.75	99.3	1.7	32.59	8.07	4.4
2014/1/28 15:22	W3	MF	832029	807886	12.4	11.900	16.6	8.75	99.3	1.6	32.59	8.07	
						1.000	16.8	8.9	112.8	2.1	32.47	8.14	4.1
						1.000	16.8	8.91	113.1	2.2	32.47	8.15	
						6.200	16.5	8.85	105.9	2.3	32.49	8.1	6.4
						6.200	16.5	8.85	105.7	2	32.49	8.1	
2014/1/28 16:04	C1	MF	833717	808190	16.3	11.400	16.5	8.72	99.1	1.5	32.58	8.07	5.0
						11.400	16.5	8.7	98.7	1.6	32.58	8.07	
						1.000	16.9	8.89	110.6	1.9	32.48	8.16	3.6
						1.000	16.9	8.89	110.8	1.7	32.48	8.16	
						8.150	16.7	8.88	109.3	2.1	32.5	8.13	3.2
2014/1/28 15:03	C2	MF	831458	807719	11	8.150	16.7	8.88	109.1	2.2	32.5	8.13	
						8.150	16.7	8.88	109.1	2.2	32.5	8.13	2.9
						15.300	16.6	8.76	102.1	2	32.56	8.09	
						15.300	16.6	8.75	101.9	2.3	32.55	8.09	
						1.000	16.9	8.87	109.4	1.7	32.47	8.15	2.7
2014/1/28 16:29	C3	MF	832234	808856	16.7	1.000	16.8	8.88	110.7	1.8	32.47	8.15	
						5.500	16.6	8.89	109.7	2.2	32.47	8.12	3.8
						5.500	16.6	8.89	109.1	2	32.47	8.12	
						10.000	16.6	8.57	100.9	2.3	32.56	8.08	3.1
						10.000	16.6	8.59	101	2.1	32.56	8.08	

MF- Mid Flood Tide  
ME- Mid Ebb tide

Contract No. DC/2009/13

Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan



Sok Kwu Wan

Date 30-Jan-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/1/30 9:00	W1	ME	832976	807724	2.6	1.300	17.8	8.66	110.8	1.7	32.53	8.16	2.2
						1.300	17.8	8.66	110.7	1.3	32.53	8.16	
2014/1/30 9:11	W2	ME	832688	807966	12.9	1.000	17.8	8.65	110.7	0.9	32.52	8.16	4.0
						1.000	17.8	8.69	111.2	1.1	32.52	8.16	
						6.450	17.8	8.68	111	1.4	32.53	8.16	3.0
						6.450	17.8	8.73	111.7	1.3	32.53	8.16	
						11.900	17.8	8.73	111.7	1.6	32.54	8.16	
11.900	17.8	8.7	111.3	1.7	32.53	8.16	3.6						
2014/1/30 9:27	W3	ME	832029	807919	12.6	1.000	17.9	8.99	114.9	1	32.28	8.17	2.4
						1.000	17.9	9	115	1	32.28	8.17	
						6.300	17.9	8.71	111.4	2.2	32.4	8.16	3.0
						6.300	17.9	8.68	111	2.3	32.38	8.16	
						11.600	17.8	8.71	111.4	2.6	32.46	8.16	3.1
						11.600	17.8	8.6	110	2.4	32.46	8.16	
2014/1/30 8:44	C1	ME	833687	808175	14.9	1.000	17.9	8.95	114.4	0.4	32.28	8.16	3.2
						1.000	17.9	8.96	114.5	0.3	32.29	8.16	
						7.450	17.8	8.75	111.9	0.9	32.47	8.15	2.3
						7.450	17.8	8.77	112.1	1.4	32.47	8.15	
						13.900	17.8	8.69	111.2	1.9	32.52	8.16	3.0
						13.900	17.8	8.67	110.9	1.4	32.52	8.15	
2014/1/30 9:42	C2	ME	831449	807724	9.8	1.000	17.8	8.67	110.9	1.8	32.43	8.16	3.8
						1.000	17.8	8.63	110.3	1.9	32.43	8.16	
						4.900	17.8	8.67	110.9	2.4	32.44	8.16	4.4
						4.900	17.8	8.64	110.5	2.2	32.44	8.16	
						8.800	17.8	8.59	109.9	2.1	32.44	8.16	3.1
						8.800	17.8	8.7	111.2	2.4	32.44	8.16	
2014/1/30 8:23	C3	ME	832246	808876	15.4	1.000	17.8	8.81	112.7	1.6	32.37	8.15	3.3
						1.000	17.8	8.81	112.6	1.7	32.35	8.16	
						7.700	17.8	8.72	111.4	2	32.36	8.15	3.2
						7.700	17.8	8.76	112	2.3	32.36	8.15	
						14.400	17.8	8.61	110.1	2.5	32.52	8.15	3.1
						14.400	17.8	8.58	109.8	2.6	32.53	8.15	
2014/1/30 12:51	W1	MF	832981	807713	2.8	1.400	17.8	8.7	111.3	1.9	32.48	8.16	3.6
						1.400	17.8	8.71	111.4	1.7	32.48	8.16	
2014/1/30 12:34	W2	MF	832676	807984	13.6	1.000	17.9	9.1	116.3	1.2	32.28	8.18	2.2
						1.000	17.9	9.1	116.4	1.4	32.28	8.18	
						6.600	17.8	8.82	112.8	1.4	32.39	8.17	3.4
						6.800	17.8	8.81	112.6	1.9	32.38	8.17	
						12.600	17.8	8.77	112.2	1.8	32.48	8.16	3.6
12.600	17.8	8.77	112.2	2	32.48	8.16							
2014/1/30 12:13	W3	MF	832033	807907	13.2	1.000	17.8	8.72	111.6	2.1	32.49	8.16	2.8
						1.000	17.8	8.71	111.3	2	32.48	8.16	
						6.600	17.8	8.8	112.6	0.8	32.42	8.16	3.0
						6.600	17.8	8.79	112.4	1.4	32.42	8.16	
						12.200	17.9	9.02	115.4	2.2	32.28	8.18	3.4
						12.200	17.9	9	115.1	1.9	32.28	8.18	
2014/1/30 13:02	C1	MF	833703	807192	16	1.000	17.9	8.95	114.4	0.5	32.28	8.18	3.8
						1.000	17.9	8.95	114.4	0.9	32.28	8.18	
						8.000	17.8	8.86	113.3	1.8	32.36	8.17	4.0
						8.000	17.8	8.84	113	1.7	32.36	8.17	
						15.000	17.8	8.77	112.2	2.2	32.48	8.16	2.8
						15.000	17.8	8.76	112.1	2.4	32.47	8.16	
2014/1/30 11:52	C2	MF	831443	807713	10.9	1.000	17.9	8.8	112.5	2.1	32.28	8.18	3.8
						1.000	17.9	8.89	113.6	2.3	32.28	8.18	
						5.450	17.9	8.81	112.6	2.6	32.33	8.17	4.7
						5.450	17.8	8.89	113.6	3.1	32.33	8.17	
						9.900	17.8	8.72	111.6	2	32.49	8.16	3.4
9.900	17.8	8.76	112	2.8	32.49	8.16							
2014/1/30 13:20	C3	MF	832216	808881	16.5	1.000	17.8	8.82	112.8	2.2	32.48	8.16	3.3
						1.000	17.8	8.77	112.2	2.1	32.48	8.16	
						8.250	17.8	8.66	110.8	2.9	32.48	8.16	3.2
						8.250	17.8	8.7	111.3	3	32.48	8.16	
						15.500	17.8	8.68	111	2.2	32.48	8.16	3.0
15.500	17.8	8.74	111.8	2.2	32.47	8.16							

MF- Mid Flood Tide  
ME- Mid Ebb tide

Contract No. DC/2009/13

Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan



Sok Kwu Wan

Date 4-Feb-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l	
			East	North										
2014/2/4 16:00	W1	ME	832977	807723	2.7	1.350	18.1	7.69	99.1	2.1	32.73	8.15	2.8	
						1.350	18.1	7.66	98.7	2.2	32.72	8.15		
2014/2/4 15:47	W2	ME	832692	807988	13.6	1.000	18	8.01	102.5	1.7	32.15	8.16	3.2	
						1.000	18	8.03	102.8	1.9	32.16	8.16		
						6.800	18.1	7.78	100.1	2.2	32.5	8.14	2.7	
						6.800	18.1	7.53	96.8	2	32.47	8.14		
						12.600	18.1	7.64	98.4	2.2	32.67	8.13		3.4
						12.600	18.1	7.67	98.8	2.3	32.72	8.14		
2014/2/4 15:30	W3	ME	832029	807896	12.8	1.000	18.6	8.08	104.7	1.7	32.03	8.17	3.0	
						1.000	18.6	8.06	104.4	1.9	32.03	8.17		
						6.400	18.1	8.32	107.1	2.2	32.6	8.16	2.6	
						6.400	18.1	8.17	105.2	2	32.59	8.15		
						11.800	18.1	7.63	98.2	2.3	32.58	8.14		3.9
						11.800	18.1	7.43	95.6	2.9	32.62	8.1		
2014/2/4 16:08	C1	ME	833713	808192	16.5	1.000	18.7	8.13	105.5	2.1	32.09	8.2	2.9	
						1.000	18.7	8.29	107.6	2.2	32.1	8.2		
						8.250	18.4	8.96	115.5	2.3	32.06	8.22	3.3	
						8.250	18.3	9.01	116	2.4	32.06	8.22		
						15.500	18.1	7.67	98.6	2.8	32.42	8.15		3.0
						15.500	18.1	7.57	97.3	2.9	32.39	8.14		
2014/2/4 15:11	C2	ME	831468	807746	10.9	1.000	18.8	7.91	102.7	3	31.98	8.16	2.9	
						1.000	18.8	7.99	103.7	3	32.01	8.16		
						5.450	18.4	8.63	111.2	2.8	32.08	8.2	3.6	
						5.450	18.4	8.63	111.3	2.7	32.07	8.21		
						9.900	18.1	8.02	103.4	1.6	32.71	8.15		3.6
						9.900	18.1	8.04	103.5	1.7	32.72	8.15		
2014/2/4 16:35	C3	ME	832238	808871	16.3	1.000	18.6	8.83	114.3	1.8	32.05	8.22	3.2	
						1.000	18.6	8.83	114.4	1.8	32.05	8.21		
						8.150	18.4	9.11	117.5	2.4	32.05	8.22	3.1	
						8.150	18.4	9.11	117.5	2.9	32.06	8.22		
						15.300	18.1	7.94	102.3	2.6	32.72	8.12		4.2
						15.300	18.1	7.98	102.7	2.4	32.7	8.13		
2014/2/4 9:34	W1	MF	832941	807720	2.8	1.400	18.1	7.79	100.4	1.9	32.74	8.14	2.1	
2014/2/4 9:43	W2	MF	832684	807979	13.9	1.000	18.7	8.21	106.4	1.9	32.06	8.18	3.7	
						1.000	18.7	8.23	106.7	2.1	32.08	8.18		
						6.600	18.1	8.54	109.5	2.2	32.13	8.19	2.8	
						6.950	18.1	8.53	109.3	2.4	32.13	8.19		
						12.900	18.1	7.52	96.8	3.1	32.69	8.08		3.1
						12.900	18.1	7.62	98.1	2.3	32.7	8.11		
2014/2/4 10:04	W3	MF	832021	807910	13.2	1.000	18.7	8.16	105.7	2.6	32.05	8.2	2.6	
						1.000	18.7	8.23	106.7	2.4	32.04	8.2		
						6.600	18.3	8.54	110	2.1	32.09	8.2	3.1	
						6.600	18.3	8.57	110.3	2	32.09	8.2		
						12.200	18.1	7.56	97.3	3.1	32.5	8.11		2.7
						12.200	18.2	7.51	96.4	3.3	32	8.11		
2014/2/4 9:22	C1	MF	833688	808119	17.1	1.000	18	8.1	103.7	0.9	32.15	8.16	3.0	
						1.000	18	8.09	103.6	1.4	32.15	8.16		
						8.550	18.1	7.93	102.1	1.3	32.74	8.15	3.5	
						8.550	18.1	7.92	102	1.6	32.74	8.15		
						16.100	18.1	7.75	99.9	1.8	32.72	8.13		2.9
						16.100	18.1	7.72	99.5	1.6	32.73	8.14		
2014/2/4 10:19	C2	MF	831447	807727	11.3	1.000	18	8.22	105.3	1.6	32.14	8.17	3.2	
						1.000	18	8.22	105.3	1.8	32.15	8.17		
						5.650	18.1	8.1	104.3	2.1	32.73	8.15	2.5	
						5.650	18.1	8.03	103.5	2.3	32.73	8.15		
						10.300	18.1	7.77	100	2.6	32.72	8.11		4.7
						10.300	18.1	7.8	100.4	2.9	32.73	8.13		
2014/2/4 9:00	C3	MF	832245	808881	16.8	1.000	18.7	8.65	112.2	1.7	32.07	8.2	2.7	
						1.000	18.7	8.66	112.3	2	32.07	8.2		
						8.400	18.4	8.9	114.9	2.3	32.07	8.21	3.2	
						8.400	18.4	8.92	115.2	2.2	32.06	8.21		
						15.800	18	8.24	105.8	2.8	32.36	8.16		3.4
						15.800	18	8.24	105.7	2.8	32.34	8.16		

MF- Mid Flood Tide  
ME- Mid Ebb tide

Contract No. DC/2009/13

Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan



Sok Kwu Wan

Date 6-Feb-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/2/6 17:52	W1	ME	832979	807724	2.6	1.300	18.2	7.72	99.5	2.2	32.7	8.15	3.0
						1.300	18.2	7.76	100	2	32.71	8.16	
2014/2/6 17:36	W2	ME	832690	807988	12.7	1.000	18.4	8.75	112.9	1.3	32.09	8.23	2.0
						1.000	18.4	8.79	113.4	1.6	32.08	8.23	2.7
						6.350	18.2	8.35	107.6	2.2	32.69	8.18	
						6.350	18.2	8.33	107.3	2.7	32.68	8.17	3.0
						11.700	18.2	7.46	95.7	2.8	32.03	8	
11.700	18.2	7.4	95	2	32.03	7.99							
2014/2/6 17:18	W3	ME	832022	807908	12.3	1.000	18.4	8.88	114.6	1.4	32.08	8.23	2.4
						1.000	18.4	8.89	114.7	1.9	32.07	8.23	3.7
						6.150	18.2	8.41	108.5	2.3	32.67	8.18	
						6.150	18.2	8.41	108.4	2.6	32.67	8.18	3.4
						11.300	18.2	7.1	91.2	2.9	32.27	7.94	
						11.300	18.2	7.04	90.5	3.1	32.27	7.93	
2014/2/6 18:02	C1	ME	833711	808193	15.9	1.000	18.4	8.36	107.8	1	32.1	8.22	3.2
						1.000	18.4	8.41	108.4	1.1	32.1	8.22	2.0
						7.950	18.2	8	103.2	2	32.71	8.17	
						7.950	18.2	8.09	104.3	1.9	32.7	8.18	2.8
						14.900	18.2	7.84	101	3.1	32.72	8.07	
14.900	18.2	7.81	100.7	3.1	32.71	8.07							
2014/2/6 17:02	C2	ME	831492	807716	10.4	1.000	18.4	8.45	109	2.3	32.07	8.23	2.2
						1.000	18.4	8.46	109.2	2.3	32.08	8.22	3.5
						5.200	18.2	8.25	106.4	2.9	32.63	8.19	
						5.200	18.2	8.27	106.5	3	32.64	8.19	3.0
						9.400	18.1	7.72	99.1	2.4	32.18	8.13	
						9.400	18.1	7.61	97.8	2.1	32.29	8.12	
2014/2/6 18:29	C3	ME	832228	808881	16.5	1.000	18.4	8.74	112.8	2	32.1	8.23	2.6
						1.000	18.4	8.76	113	1.6	32.09	8.23	2.8
						8.250	18.2	8.45	109	1.9	32.67	8.19	
						8.250	18.2	8.42	108.6	2.4	32.68	8.19	2.2
						15.500	18.2	7.89	101.7	2.2	32.71	8.14	
						15.500	18.2	7.88	101.6	2.9	32.73	8.15	
2014/2/6 10:51	W1	MF	832944	807713	2.8	1.400	18.1	8.11	104.4	2.3	32.64	8.16	2.8
						1.400	18.1	8.09	104.1	2.7	32.64	8.16	
2014/2/6 11:03	W2	MF	832692	807999	13.3	1.000	18.1	8.4	108.1	2.1	32.52	8.18	3.6
						1.000	18.1	8.41	108.2	1.9	32.54	8.19	3.0
						6.300	18.1	8.09	104.3	2	32.67	8.15	
						6.650	18.1	7.96	102.6	2.6	32.73	8.15	2.1
						12.300	18.1	8.05	103.7	1.9	32.69	8.16	
12.300	18.1	8.08	104.1	2.5	32.69	8.16							
2014/2/6 11:20	W3	MF	832016	807863	12.6	1.000	18.1	8.07	104	0.9	32.69	8.16	3.0
						1.000	18.1	8.07	103.9	1.4	32.69	8.16	2.9
						6.300	18.1	8.45	108.7	1.9	32.52	8.19	
						6.300	18.1	8.47	109	1.6	32.53	8.19	2.8
						11.600	18.2	8.48	109.2	1.7	32.55	8.19	
						11.600	18.2	8.48	109.3	0.8	32.57	8.19	
2014/2/6 10:38	C1	MF	833701	808176	16.3	1.000	18.1	7.9	101.7	1.6	32.65	8.17	3.2
						1.000	18.1	7.86	101.3	1.7	32.65	8.17	2.7
						8.150	18.1	8.05	103.7	2.2	32.62	8.17	
						8.150	18.1	8.14	104.8	2.6	32.58	8.17	2.8
						15.300	18.1	8.09	104.2	2.3	32.66	8.16	
15.300	18.1	8.09	104.1	2.6	32.65	8.16							
2014/2/6 11:32	C2	MF	831492	807728	11	1.000	18.2	8.17	105.2	2.2	32.65	8.17	2.6
						1.000	18.2	8.16	105.1	2.2	32.66	8.17	2.5
						5.500	18	8.69	111.5	2.4	32.29	8.2	
						5.500	18	8.71	111.7	2.1	32.29	8.2	3.1
						10.000	18.2	8.16	105.2	2.9	32.69	8.16	
10.000	18.2	8.17	105.3	2.8	32.68	8.16							
2014/2/6 10:18	C3	MF	832228	808879	16.8	1.000	18.1	8.31	107	2.1	32.58	8.17	3.1
						1.000	18.1	8.25	106.1	2.2	32.6	8.17	3.5
						8.400	18.1	7.84	100.9	2.4	32.64	8.15	
						8.400	18.1	7.91	101.9	2.5	32.63	8.15	3.0
						15.800	18.1	7.87	101.3	2.6	32.64	8.16	
15.800	18.1	7.86	101.2	2.7	32.65	8.16							

MF- Mid Flood Tide  
ME- Mid Ebb tide

Contract No. DC/2009/13

Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan



Sok Kwu Wan

Date 8-Feb-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/2/8 17:58	W1	ME	832977	807738	2.7	1.350	15.8	8.7	106.7	1.6	32.55	8.17	2.3
						1.350	15.8	8.71	105.7	1.7	32.56	8.17	
2014/2/8 17:45	W2	ME	832678	807994	12.4	1.000	15.8	9.1	106.3	0.8	32.48	8.17	2.3
						1.000	15.8	9.1	106.5	0.6	32.5	8.17	
						6.200	15.7	8.82	105.1	1.3	32.64	8.16	2.3
						6.200	15.7	8.81	105.3	1	32.63	8.16	
						11.400	15.6	8.77	103.3	0.7	32.76	8.15	
11.400	15.6	8.77	103.6	0.9	32.75	8.15	3.0						
2014/2/8 17:22	W3	ME	832068	807908	12	1.000	15.9	8.72	105.7	1.3	32.48	8.17	2.2
						1.000	15.9	8.71	106.1	1.6	32.47	8.17	
						6.000	15.9	8.8	104.6	0.8	32.64	8.17	1.9
						6.000	15.9	8.79	104.1	0.9	32.63	8.16	
						11.000	15.7	9.02	102.3	1.1	32.75	8.16	3.1
						11.000	15.7	9	102.9	1.5	32.75	8.16	
2014/2/8 18:12	C1	ME	833694	808190	15.6	1.000	15.8	8.95	107	0.7	32.56	8.17	2.9
						1.000	15.8	8.95	107	1.4	32.58	8.17	
						7.800	15.7	8.86	105.8	1.8	32.65	8.17	3.0
						7.800	15.7	8.84	105.9	1.8	32.65	8.17	
						14.600	15.6	8.77	104.1	0.4	32.75	8.16	2.2
						14.600	15.6	8.76	104	0.2	32.76	8.16	
2014/2/8 17:02	C2	ME	831467	807716	9.9	1.000	15.9	8.8	105.7	0.9	32.43	8.17	2.8
						1.000	15.8	8.89	106	1	32.42	8.17	
						4.950	15.8	8.81	105.5	0.8	32.64	8.16	3.7
						4.950	15.7	8.89	105.5	0.6	32.64	8.16	
						8.900	15.7	8.72	102.6	1.3	32.74	8.15	3.1
						8.900	15.7	8.76	102.4	1.6	32.75	8.16	
2014/2/8 18:33	C3	ME	832249	808884	16.3	1.000	15.9	8.82	103.8	2	32.45	8.17	3.8
						1.000	15.9	8.77	104.7	2.1	32.5	8.17	
						8.150	15.8	8.66	104.3	2.4	32.65	8.17	4.3
						8.150	15.7	8.7	104.1	2	32.65	8.17	
						15.300	15.6	8.68	103.5	1.3	32.75	8.16	4.5
						15.300	15.6	8.74	102.4	1.9	32.75	8.16	
2014/2/8 12:49	W1	MF	832984	807704	2.8	1.400	16.5	8.73	106.3	2.4	32.22	8.17	4.8
						1.400	16.5	8.7	105.4	2.1	32.22	8.17	
2014/2/8 12:35	W2	MF	832694	807971	12.6	1.000	16.5	8.66	102.4	0.9	32.22	8.15	2.4
						1.000	16.5	8.66	102.6	0.9	32.21	8.15	
						6.000	16.5	8.65	105.7	1.2	32.44	8.15	1.7
						6.300	16.5	8.69	105.6	1.1	32.44	8.16	
						11.600	16.4	8.68	102.2	0.9	32.63	8.14	2.6
11.600	16.4	8.73	102.1	1	32.63	8.14							
2014/2/8 12:10	W3	MF	832025	807884	12	1.000	16.6	8.95	101.2	2.4	32.22	8.14	2.6
						1.000	16.6	8.96	102.1	2.4	32.23	8.14	
						6.000	16.5	8.75	103.8	1.8	32.48	8.14	4.2
						6.000	16.5	8.77	103.8	1.3	32.48	8.14	
						11.000	16.4	8.69	101	2	32.55	8.12	2.9
						11.000	16.4	8.67	102.2	2.7	32.55	8.13	
2014/2/8 13:01	C1	MF	833690	808180	15.8	1.000	16.5	8.99	104.3	0.9	32.38	8.17	3.8
						1.000	16.5	9	104.6	1	32.37	8.17	
						7.900	16.4	8.71	104.9	1.1	32.63	8.16	4.4
						7.900	16.4	8.68	104.9	1.9	32.63	8.16	
						14.800	16.4	8.71	106	1.3	32.62	8.16	3.4
						14.800	16.4	8.6	106	1.6	32.62	8.16	
2014/2/8 11:48	C2	MF	831491	807769	10.2	1.000	16.6	8.81	105.7	0.3	32.24	8.12	2.2
						1.000	16.6	8.81	105.9	1.4	32.25	8.12	
						5.100	16.6	8.72	101.5	2.1	32.27	8.13	3.0
						5.100	16.6	8.76	102	1.8	32.27	8.13	
						9.200	16.5	8.61	100.7	2.2	32.41	8.13	3.3
						9.200	16.4	8.58	97.9	1.7	32.47	8.13	
2014/2/8 13:27	C3	MF	832260	808819	16.4	1.000	16.5	8.67	104.7	0.9	32.46	8.17	2.6
						1.000	16.5	8.63	105.8	0.8	32.47	8.17	
						8.200	16.4	8.67	104.2	1.3	32.63	8.16	2.5
						8.200	16.4	8.64	104.3	1.6	32.63	8.16	
						15.400	16.4	8.59	103	2	32.74	8.15	2.2
						15.400	16.4	8.7	102.9	2	32.74	8.15	

MF- Mid Flood Tide  
ME- Mid Ebb tide



Contract No. DC/2009/13

**Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan**



**Sok Kwu Wan**

Date 10-Feb-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/2/10 17:53	W1	ME	832971	807719	2.7	1.350	13.5	8.08	83.9	1.8	33.04	8.04	1.7
						1.350	13.5	8.06	83.6	0.9	33.03	8.04	
2014/2/10 17:37	W2	ME	832691	807994	12.9	1.000	13.8	7.83	83.4	0.8	33.04	8.04	2.2
						1.000	13.8	7.81	83.6	0.9	33.04	8.05	
						6.450	13.7	7.91	83.5	1.2	33.04	8.05	2.6
						6.450	13.7	7.99	83.5	1.1	33.04	8.05	
						11.900	13.5	8.63	83.5	1.8	33.03	8.05	
						11.900	13.5	8.63	83.5	1.7	33.04	8.05	
2014/2/10 17:21	W3	ME	832026	807891	12.4	1.000	13.9	8.34	81.6	2.1	33.02	8.04	2.2
						1.000	13.9	8.31	81.3	1.8	33.02	8.04	
						6.200	13.7	7.71	82.8	2.2	33.04	8.06	2.4
						6.200	13.7	7.64	83.2	2	33.04	8.05	
						11.400	13.7	7.34	83.1	1.3	33.02	8.05	
						11.400	13.7	7.62	82.5	1.3	33.02	8.04	
2014/2/10 18:06	C1	ME	833713	808192	16.5	1.000	13.7	7.63	83.8	0.3	33.04	8.05	2.3
						1.000	13.7	7.43	83.9	0.2	33.04	8.05	
						8.250	13.7	8.01	84	0.8	33.03	8.05	3.5
						8.250	13.7	8.03	84	0.9	33.03	8.05	
						15.500	13.6	7.78	84.5	1	33.04	8.05	
						15.500	13.6	7.53	84.3	1.1	33.04	8.06	
2014/2/10 17:06	C2	ME	831468	807719	10.7	1.000	13.9	8.65	83.1	0.4	33.03	8.05	3.7
						1.000	13.9	8.69	83.2	0.9	33.03	8.05	
						5.350	13.8	8.6	82.8	1.2	33.03	8.05	4.4
						5.350	13.8	8.62	83.1	1.3	33.03	8.05	
						9.700	13.8	8.46	84.4	0.8	33.02	8.04	
						9.700	13.8	8.46	84.1	1.4	33.02	8.04	
2014/2/10 18:25	C3	ME	832228	808871	16.8	1.000	13.7	7.64	84.2	0.2	33.04	8.05	4.0
						1.000	13.7	7.67	84.3	0.3	33.04	8.05	
						8.400	13.7	7.69	84.9	1.3	33.04	8.05	2.5
						8.400	13.7	7.66	84.6	1.9	33.04	8.05	
						15.800	13.6	8.13	84.7	1.4	33.04	8.06	
						15.800	13.6	8.29	85	1.6	33.03	8.06	
2014/2/10 10:21	W1	MF	832964	807738	2.8	1.400	14.3	7.52	82.9	0.7	32.99	8.04	2.0
						1.400	14.3	7.62	83.1	0.9	32.99	8.02	
2014/2/10 10:08	W2	MF	832673	807995	13.2	1.000	14.2	7.79	82	1.3	33.04	8.06	4.8
						1.000	14.2	7.77	82.1	1.6	33.04	8.06	
						6.350	14.1	8.21	82.8	2	33.04	8.06	2.0
						6.600	14.1	8.23	82.8	2.1	33.04	8.06	
						12.200	14.2	8.54	83.2	3.2	33	8.06	
						12.200	14.1	8.53	83	2.9	33.01	8.06	
2014/2/10 9:49	W3	MF	832024	807897	12.7	1.000	14.3	8.1	82.2	1.8	33.04	8.05	2.2
						1.000	14.3	8.09	82.5	1.9	33.04	8.05	
						6.350	14.2	7.93	82.6	2	33.04	8.06	2.2
						6.350	14.2	7.92	82.5	2.4	33.04	8.06	
						11.700	14.1	7.75	82.9	2.1	33.04	8.06	
						11.700	14.1	7.72	82.3	2	33.04	8.06	
2014/2/10 10:28	C1	MF	833709	808192	16.4	1.000	14.2	8.16	83.1	0.4	33.01	8.02	2.7
						1.000	14.2	8.23	82.9	0.9	33.03	8.02	
						8.200	14.1	8.54	83.5	1.3	33.03	8.04	3.1
						8.200	14.1	8.57	83.4	1.6	33.03	8.04	
						15.400	14.1	7.56	83.6	2.4	33.03	8.05	
						15.400	14.1	7.51	83.6	2	33.03	8.05	
2014/2/10 9:36	C2	MF	831497	807719	11	1.000	14.2	8.65	80.6	0.4	33.02	8.04	2.9
						1.000	14.2	8.66	80.6	0.9	33.02	8.05	
						5.500	14.2	8.9	82	1	33.04	8.05	5.0
						5.500	14.2	8.92	81.9	1.3	33.04	8.05	
						10.000	14	8.24	81.8	1.8	33.03	8.06	
						10.000	14	8.24	81.4	1.6	33.03	8.05	
2014/2/10 10:49	C3	MF	832224	808882	17	1.000	14.2	8.22	82.2	0.3	33.01	8.03	3.7
						1.000	14.2	8.22	82.2	0.9	33.01	8.03	
						8.500	14.2	8.1	83.3	0.9	33.03	8.05	4.5
						8.500	14.2	8.03	83	0.8	33.02	8.05	
						16.000	14.1	7.77	82.6	1.3	33.03	8.05	
						16.000	14.1	7.8	82.6	1.6	33.03	8.05	

MF- Mid Flood Tide  
ME- Mid Ebb tide

Contract No. DC/2009/13

Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan



Sok Kwu Wan

Date 12-Feb-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/2/12 11:04	W1	ME	832964	807716	2.6	1.300	13.1	7.84	87.5	1.3	33.22	8.06	5.5
						1.300	13.1	7.91	87.5	2	33.22	8.06	
2014/2/12 11:15	W2	ME	832680	807997	13	1.000	13.1	7.87	88.2	1.5	33.22	8.06	4.4
						1.000	13.1	7.86	88.1	1.7	33.22	8.06	
						6.500	13.1	7.9	88	1.9	33.23	8.06	3.7
						6.500	13.1	7.86	88	1.9	33.23	8.06	
						12.000	13	8.05	86.4	2	33.22	8.06	
						12.000	12.9	8.14	86.9	2	33.22	8.06	
2014/2/12 11:32	W3	ME	832045	807890	12.6	1.000	13	8.09	86.4	0.9	33.22	8.06	3.3
						1.000	12.9	8.09	86.7	0.7	33.21	8.06	
						6.300	12.9	8.11	86.4	1.5	33.22	8.06	3.9
						6.300	12.9	8.09	86.4	1.7	33.22	8.06	
						11.600	12.9	8.4	86.8	2.4	33.22	8.06	
						11.600	12.9	8.41	86.8	2.3	33.22	8.06	
2014/2/12 10:53	C1	ME	833694	808194	16	1.000	13.1	9.11	86.9	0.3	33.21	8.05	3.8
						1.000	13.1	9.11	87.9	0.5	33.21	8.05	
						8.000	13.1	7.94	86.8	0.8	33.22	8.05	3.1
						8.000	13.1	7.98	86.7	0.8	33.21	8.05	
						15.000	13	8.31	86.3	1	33.21	8.06	
						15.000	13	8.25	86.9	1.1	33.23	8.06	
2014/2/12 11:45	C2	ME	831468	807765	10.4	1.000	13.1	8.09	89.2	0.7	33.23	8.06	3.7
						1.000	13.1	7.96	89.1	0.8	33.23	8.06	
						5.200	13.1	8.05	87.5	1.1	33.22	8.06	4.2
						5.200	13.1	8.08	87.6	1.1	33.22	8.06	
						9.400	12.9	8.07	87.1	2.1	33.21	8.06	
						9.400	12.9	8.07	87.1	1.3	33.21	8.06	
2014/2/12 10:35	C3	ME	832239	808846	16.8	1.000	13.1	8.96	85.1	0.9	33.2	8.06	2.8
						1.000	13.1	9.01	85	1.4	33.21	8.06	
						8.400	13	7.67	86.2	1.6	33.21	8.05	3.8
						8.400	13	7.57	86.2	1.7	33.21	8.05	
						15.800	13	8.83	85.4	2.4	33.2	8.05	
						15.800	13	8.83	85.4	2	33.2	8.05	
2014/2/12 16:32	W1	MF	832967	807744	2.8	1.400	13.2	7.1	85.3	1.9	33.15	8.03	2.9
						1.400	13.2	7.04	85.2	1.8	33.15	8.03	
2014/2/12 16:20	W2	MF	832690	807969	13.6	1.000	13	7.72	87.8	2	33.2	8.06	3.7
						1.000	13	7.61	87.8	2.1	33.2	8.06	
						6.450	13	8.88	88.2	0.9	33.19	8.06	3.0
						6.800	13	8.89	88.1	1.1	33.2	8.06	
						12.600	13.2	8.41	87	2.1	33.15	8.03	
						12.600	13.2	8.41	86.8	2	33.15	8.03	
2014/2/12 16:04	W3	MF	832039	807916	12.9	1.000	13	8.69	88	0.9	33.2	8.07	3.7
						1.000	13	8.71	88.1	1	33.2	8.06	
						6.450	13	8.16	88.2	1.3	33.2	8.06	3.8
						6.450	13	8.17	87.9	1.9	33.2	8.06	
						11.900	13	8.45	88.1	2	33.19	8.06	
						11.900	13	8.46	88.1	1.9	33.19	8.06	
2014/2/12 16:37	C1	MF	833692	808173	16.4	1.000	13.2	8.75	85.1	1	33.15	8.03	5.2
						1.000	13.2	8.79	85.2	1	33.15	8.03	
						8.200	13.2	8.35	85.2	2	33.15	8.03	5.4
						8.200	13	8.33	84.9	1.8	33.15	8.03	
						15.400	13	7.46	85.4	1.6	33.16	8.04	
						15.400	13	7.4	85.2	1.6	33.16	8.04	
2014/2/12 15:50	C2	MF	831471	807729	11	1.000	13.2	8.45	89.6	0.7	33.2	8.05	4.2
						1.000	13.2	8.47	89.7	0.8	33.2	8.06	
						5.500	13.2	8.48	87.7	0.9	33.2	8.06	3.6
						5.500	13.2	8.48	87.8	0.9	33.2	8.06	
						10.000	13	8.17	87.7	1.4	33.19	8.06	
						10.000	13	8.16	87.8	1.5	33.2	8.06	
2014/2/12 16:52	C3	MF	832243	808861	17.1	1.000	13.1	7.72	86.1	2	33.17	8.04	6.2
						1.000	13.1	7.76	86	1.6	33.17	8.04	
						8.550	12.9	8.36	86.1	2	33.16	8.04	5.5
						8.550	12.9	8.41	86.1	1.9	33.17	8.04	
						16.100	12.9	8	85.7	0.4	33.17	8.04	
						16.100	12.9	8.09	85.7	0.2	33.17	8.04	

MF- Mid Flood Tide

ME- Mid Ebb tide

Contract No. DC/2009/13

Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan



Sok Kwu Wan

Date 15-Feb-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/2/15 8:51	W1	ME	832988	807717	2.8	1.400	14.1	7.58	85.6	0.7	33.19	8.05	5.6
						1.400	14.1	7.56	85.8	0.8	33.2	8.05	
2014/2/15 9:11	W2	ME	832695	808007	12.6	1.000	14.3	8.02	87.2	1.3	33.19	8.05	3.2
						1.000	14.3	8.02	87.4	1	33.19	8.05	
						6.300	14.1	7.71	85.7	0.4	33.19	8.05	3.7
						6.300	14.1	7.7	85.7	0.3	33.19	8.05	
						11.600	14	7.62	84.7	1.2	33.19	8.05	
11.600	14	7.63	84.8	1.9	33.2	8.06	3.0						
2014/2/15 8:23	W3	ME	832022	807908	11.8	1.000	14.2	8.16	87.8	1.2	33.19	8.06	3.4
						1.000	14.2	8.15	88.2	1.3	33.2	8.05	
						5.900	14.1	7.9	86.7	0.5	33.19	8.06	3.8
						5.900	14.1	7.89	86.8	0.7	33.2	8.06	
						10.800	14	8.21	89	0.8	33.21	8.06	3.1
						10.800	14	8.14	89.1	0.3	33.22	8.06	
2014/2/15 8:39	C1	ME	833684	808179	15.9	1.000	14.2	7.89	85.8	1.3	33.16	8.04	3.3
						1.000	14.2	7.88	85.5	1.6	33.16	8.04	
						7.950	14.1	8.16	86.4	1.7	33.19	8.05	2.8
						7.950	14.1	8.17	86.4	1.9	33.2	8.05	
						14.900	14	7.83	87.4	2.2	33.2	8.06	2.2
						14.900	14	7.87	87.5	2.3	33.2	8.06	
2014/2/15 8:40	C2	ME	831468	807729	9.8	1.000	14.1	8.36	88.3	1.8	33.18	8.07	2.9
						1.000	14.1	8.29	87.9	1.4	33.18	8.07	
						4.900	14.1	8.06	84.4	0.8	33.18	8.05	3.0
						4.900	14.1	8.05	84.6	0.7	33.19	8.06	
						8.800	14.1	7.63	81.5	1.7	33.18	8.06	3.0
						8.800	14.1	7.61	81.6	1.9	33.18	8.06	
2014/2/15 8:22	C3	ME	832237	808876	16.2	1.000	14.2	8.84	88.2	0.2	33.17	8.04	2.2
						1.000	14.2	8.81	88.4	0.6	33.17	8.04	
						8.100	14.2	8.74	85.6	1.4	33.17	8.04	2.7
						8.100	14.2	8.76	85.5	0.8	33.17	8.04	
						15.200	14.1	8.45	82.7	1.7	33.17	8.04	3.0
						15.200	14.1	8.52	83.8	1.1	33.17	8.04	
2014/2/15 12:58	W1	MF	832953	807749	2.8	1.400	14	7.85	83.8	1	33.2	8.07	2.7
						1.400	14	7.85	83.8	0.7	33.2	8.07	
2014/2/15 12:46	W2	MF	832692	807990	13	1.000	14.2	8.21	88.6	1.1	33.2	8.07	3.0
						1.000	14.2	8.23	88.6	1.2	33.2	8.07	
						6.250	14.2	8.12	86.6	0.9	33.2	8.07	2.4
						6.500	14.2	8.14	86.7	0.7	33.2	8.07	
						12.000	14.1	7.99	84.6	2	33.2	8.07	2.8
12.000	14.1	8.01	84.7	1.6	33.2	8.07							
2014/2/15 12:32	W3	MF	832016	807908	12.5	1.000	14.3	8.16	88.9	1.3	33.2	8.07	4.4
						1.000	14.3	8.2	88.9	0.9	33.2	8.07	
						6.250	14.3	8.08	86.8	1.1	33.19	8.06	2.7
						6.250	14.3	8.05	86.6	1.4	33.2	8.06	
						11.500	14.1	7.91	85.6	0.9	33.19	8.06	4.8
						11.500	14.1	7.95	85.6	1.3	33.19	8.06	
2014/2/15 13:05	C1	MF	833693	808188	16.2	1.000	14.2	8.27	89	0.6	33.2	8.07	2.4
						1.000	14.2	8.27	89.1	0.7	33.2	8.07	
						8.100	14.2	7.98	86.1	1.2	33.2	8.07	2.2
						8.100	14.2	7.98	86.2	1.6	33.2	8.07	
						15.200	14	7.65	82.3	2	33.2	8.07	2.4
						15.200	14	7.64	82.4	1.4	33.2	8.07	
2014/2/15 12:14	C2	MF	831461	807727	10.7	1.000	14.1	8.36	88.3	1.4	33.18	8.07	4.1
						1.000	14.1	8.29	87.9	1.5	33.18	8.07	
						5.350	14.1	8.06	84.4	0.3	33.18	8.05	3.8
						5.350	14.1	8.05	84.6	0.8	33.19	8.06	
						9.700	14.1	7.63	81.5	1.6	33.18	8.06	2.1
						9.700	14.1	7.61	81.6	1.5	33.18	8.06	
2014/2/15 13:24	C3	MF	832239	808881	16.7	1.000	14.1	8.09	88.5	1.1	33.19	8.06	2.8
						1.000	14.1	8.06	88.4	1.3	33.19	8.06	
						8.350	14.1	7.75	85.3	1.2	33.19	8.06	2.9
						8.350	14	7.76	85.3	1.7	33.19	8.06	
						15.700	14	7.41	80.8	2.4	33.2	8.06	6.3
15.700	14	7.4	80.7	2.1	33.19	8.06							

MF- Mid Flood Tide  
ME- Mid Ebb tide

Contract No. DC/2009/13

Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan



Sok Kwu Wan

Date 18-Feb-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/2/18 14:48	W1	ME	832982	807718	2.8	1.400	17	6.63	90.4	1.3	33.21	8.06	4.0
						1.400	17	6.63	90.4	1.2	33.21	8.06	
2014/2/18 14:36	W2	ME	832684	807999	11.8	1.000	17.1	6.62	90.2	0.8	33.22	8.06	4.6
						1.000	17.1	6.59	90.2	0.9	33.23	8.06	
						5.900	17.1	6.56	88.2	0.7	33.22	8.06	4.6
						5.900	17	6.57	88.3	0.7	33.22	8.06	
						10.800	17	6.61	86.3	1.3	33.21	8.06	
						10.800	17	6.62	86.4	1.6	33.21	8.06	
2014/2/18 14:25	W3	ME	832039	807892	12.4	1.000	17.2	6.58	89.6	0.8	33.22	8.06	3.6
						1.000	17.2	6.59	89.6	0.9	33.22	8.06	
						6.200	17	6.39	87.6	1.1	33.22	8.06	3.5
						6.200	17	6.38	87.6	1.3	33.22	8.06	
						11.400	17	6.29	83.7	1.4	33.22	8.06	
						11.400	17	6.28	83.7	1.6	33.22	8.06	
2014/2/18 14:56	C1	ME	833708	808190	15.4	1.000	17.2	6.66	90.2	0.8	33.22	8.06	4.4
						1.000	17.2	6.65	90.2	1.4	33.22	8.06	
						7.700	17	6.44	88.3	0.9	33.21	8.06	5.1
						7.700	17	6.45	88.3	1.2	33.21	8.06	
						14.400	17	6.39	85.4	1.6	33.22	8.06	
						14.400	17	6.37	85.5	1.8	33.22	8.06	
2014/2/18 14:11	C2	ME	831467	807748	10.3	1.000	17	6.64	89.6	0.9	33.23	8.06	3.8
						1.000	17	6.44	89.5	1	33.23	8.06	
						5.150	17	6.32	87.6	1.6	33.22	8.06	4.2
						5.150	17	6.33	87.6	1.6	33.22	8.06	
						9.300	17	6.36	87.5	1.9	33.22	8.06	
						9.300	17	6.35	87.5	1.4	33.22	8.06	
2014/2/18 15:19	C3	ME	832218	808818	15.8	1.000	17	6.68	90.4	1.9	33.22	8.06	3.8
						1.000	17	6.7	90.5	2	33.22	8.06	
						7.900	17	6.72	90.4	1.8	33.21	8.06	3.1
						7.900	17	6.71	90.2	1.7	33.22	8.06	
						14.800	17	6.82	89.9	1.4	33.22	8.06	
						14.800	17	6.81	90.1	1.6	33.22	8.06	
2014/2/18 8:43	W1	MF	832969	807722	2.8	1.400	17.1	6.57	88.2	0.8	33.22	8.06	4.9
2014/2/18 8:59	W2	MF	832683	808003	12.3	1.400	17.1	6.55	88.1	0.6	33.22	8.06	4.2
						1.000	17.2	7.44	91.5	0.9	33.21	8.06	
						1.000	17.2	7.46	91.7	1.2	33.21	8.06	5.0
						6.500	17.1	6.56	87.8	1.3	33.22	8.05	
						6.150	17.1	6.54	87.8	1.6	33.22	8.06	
						11.300	17	6.29	83.9	0.5	33.22	8.06	
2014/2/18 9:12	W3	MF	832039	807894	13	11.300	17	6.28	83.8	0.7	33.21	8.06	4.3
						1.000	17.1	6.62	89.4	0.8	33.23	8.06	
						1.000	17.1	6.63	89.5	0.7	33.22	8.06	4.1
						6.500	17	6.49	86.5	1.2	33.22	8.06	
						6.500	17	6.49	86.5	1.9	33.21	8.06	
						12.000	17	6.37	85.5	2	33.21	8.06	
2014/2/18 8:29	C1	MF	833708	808180	16	12.000	17	6.35	85.5	1.8	33.22	8.06	5.1
						1.000	17.1	7.91	93.7	0.3	33.22	8.05	
						1.000	17.1	7.91	93.7	0.6	33.22	8.05	3.5
						8.000	17.1	7.34	91	0.9	33.22	8.06	
						8.000	17.1	7.29	91	0.9	33.22	8.06	
						15.000	17	6.46	88.9	1.1	33.22	8.06	
2014/2/18 9:26	C2	MF	831468	807716	11.1	15.000	17	6.48	88.6	1.2	33.21	8.06	3.0
						1.000	17.2	6.52	88.8	0.3	33.21	8.06	
						1.000	17.2	6.52	88.7	0.2	33.22	8.06	4.5
						5.550	17	6.26	85.7	0.6	33.22	8.06	
						5.550	17	6.26	85.7	0.7	33.22	8.06	
						10.100	17	6.03	82.6	1.2	33.22	8.06	
2014/2/18 8:12	C3	MF	832244	808893	16.5	10.100	17	6.06	82.6	1.9	33.22	8.06	5.0
						1.000	17.2	8.47	95.8	1.2	33.22	8.05	
						1.000	17.2	8.46	95.7	1.4	33.22	8.05	4.5
						8.250	17	7.45	92.8	2	33.23	8.05	
						8.250	17	7.42	92.1	2	33.22	8.05	
						15.500	17	6.48	88.3	1.6	33.21	8.05	
15.500	17	6.51	88.4	1.8	33.22	8.05	4.8						

MF- Mid Flood Tide  
ME- Mid Ebb tide

Contract No. DC/2009/13

**Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan**

**Sok Kwu Wan**

Date 20-Feb-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/2/20 15:39	W1	ME	832971	807747	2.7	1.350	13.1	7.62	84.3	1.1	33.19	8.07	3.6
						1.350	13.1	7.55	83.8	1.7	33.19	8.07	
2014/2/20 15:30	W2	ME	832694	807991	13.1	1.000	13.1	7.64	84	0.9	33.18	8.05	4.1
						1.000	13.1	7.67	83.4	1.3	33.18	8.06	
						6.550	13	7.54	82.1	1.5	33.18	8.06	3.6
						6.550	13	7.5	82.3	1.8	33.18	8.05	
						12.100	13	7.48	81.4	1.6	33.17	8.06	
						12.100	13	7.42	81.1	1.2	33.17	8.06	
2014/2/20 15:19	W3	ME	832021	807916	12.6	1.000	13.2	8.07	91.2	0.8	33.2	8.07	4.4
						1.000	13.2	8.04	90.4	0.7	33.2	8.06	
						6.300	13.2	7.88	87.2	1.4	33.2	8.06	3.6
						6.300	13.2	7.85	87	1.4	33.2	8.06	
						11.600	13	7.78	86.1	2.1	33.19	8.06	
						11.600	13	7.8	86.3	1.8	33.19	8.06	
2014/2/20 15:48	C1	ME	833694	808180	15.8	1.000	13.2	7.58	86.2	0.9	33.2	8.07	3.7
						1.000	13.2	7.52	86	1	33.2	8.07	
						7.900	13.2	7.48	83.9	1	33.18	8.07	4.6
						7.900	13.1	7.43	83.3	1.7	33.18	8.06	
						14.800	13.1	7.37	82.4	1.7	33.17	8.06	3.0
						14.800	13.1	7.31	82	1.8	33.17	8.06	
2014/2/20 15:07	C2	ME	831468	807719	108	1.000	13.1	7.82	88.4	0.8	33.19	8.06	4.4
						1.000	13.1	7.75	86.7	0.7	33.19	8.05	
						54.000	13	7.52	85.1	1.2	33.17	8.06	4.9
						54.000	13	7.5	84.7	1.3	33.17	8.06	
						107.000	13	7.33	82	1.8	33.17	8.05	3.2
						107.000	13	7.33	82.4	1.4	33.17	8.06	
2014/2/20 16:19	C3	ME	832228	808881	16.4	1.000	13.3	7.6	82.6	2.1	33.17	8.05	3.8
						1.000	13.3	7.51	81.8	2.2	33.17	8.05	
						8.200	13.2	7.44	79.3	2	33.16	8.05	4.6
						8.200	13.2	7.38	79.4	1.3	33.16	8.05	
						15.400	13.2	7.2	76.8	1.6	33.16	8.05	4.6
						15.400	13.2	7.22	76.8	1.9	33.16	8.06	
2014/2/20 9:19	W1	MF	832994	907752	2.8	1.400	13.3	7.32	85.7	1.6	33.18	8.06	4.2
						1.400	13.3	7.25	86.2	1.4	33.17	8.06	
2014/2/20 9:27	W2	MF	832692	807981	13.9	1.000	13.4	7.84	93.5	0.8	33.18	8.06	3.8
						1.000	13.4	7.58	90.5	1.1	33.18	8.06	
						6.550	13.3	7.38	84.6	2.1	33.18	8.06	3.5
						6.950	13.3	7.32	84.3	2	33.2	8.06	
						12.900	13.1	7.64	89.1	2.4	33.2	8.06	
2014/2/20 9:41	W3	MF	832026	807890	13.1	1.000	13.3	7.78	95.6	0.7	33.18	8.08	3.8
						1.000	13.3	7.81	97.1	0.8	33.18	8.08	
						6.550	13.2	7.57	92.5	2.1	33.19	8.08	3.4
						6.550	13.2	7.52	91	2	33.19	8.08	
						12.100	13.2	7.48	88.8	1.5	33.19	8.08	5.5
						12.100	13.2	7.43	88.2	1.9	33.19	8.08	
2014/2/20 9:08	C1	MF	833708	808186	16	1.000	13.2	8.01	96.1	1.8	33.18	8.07	3.0
						1.000	13.2	7.86	95.7	1.5	33.18	8.07	
						8.000	13.2	7.56	91.8	0.7	33.2	8.07	4.4
						8.000	13.1	7.53	90.5	0.9	33.2	8.07	
						15.000	13.1	7.26	79.3	1.3	33.2	8.07	4.0
15.000	13.1	7.24	78.5	1.3	33.18	8.07							
2014/2/20 9:58	C2	MF	831472	807716	11.3	1.000	13.1	7.82	93.5	0.9	33.18	8.06	4.0
						1.000	13.1	7.72	91.5	0.9	33.18	8.06	
						5.650	13.1	7.53	88.6	1.4	33.17	8.06	4.0
						5.650	13.1	7.38	85.7	1.5	33.17	8.06	
						10.300	13	7.22	83.5	1.6	33.17	8.06	4.0
10.300	13	7.15	83.2	1.3	33.17	8.06							
2014/2/20 8:47	C3	MF	832249	807871	16.8	1.000	13.4	7.51	93.1	0.8	33.18	8.06	5.1
						1.000	13.4	7.51	93	0.7	33.18	8.06	
						8.400	13.4	7.45	88.4	1.6	33.19	8.06	5.2
						8.400	13.4	7.42	88.1	1.5	33.18	8.06	
						15.800	13.3	7.37	87.6	1.8	33.18	8.06	7.0
						15.800	13.3	7.35	87.2	1.9	33.19	8.06	

MF- Mid Flood Tide  
ME- Mid Ebb tide

Contract No. DC/2009/13

Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan



Sok Kwu Wan

Date 22-Feb-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/2/22 17:48	W1	ME	832981	807722	2.8	1.400	15.95	10.2	128	1.4	35.3	8.27	2.8
						1.400	15.92	10.23	128.3	1.1	35.31	8.27	
2014/2/22 17:34	W2	ME	832683	807996	12.9	1.000	15.91	10.57	132.5	2	35.24	8.3	2.5
						1.000	15.91	10.53	132	1.4	35.26	8.3	
						6.450	15.89	10.42	130.5	0.4	35.24	8.27	4.5
						6.450	15.89	10.42	130.6	0.3	35.22	8.27	
						11.900	15.84	10.45	130.8	0.6	35.22	8.25	
11.900	15.84	10.53	131.8	0.7	35.19	8.23							
2014/2/22 17:18	W3	ME	832024	807896	12.2	1.000	15.86	10.03	125.6	1.2	35.24	8.19	3.8
						1.000	15.86	10.06	126	1.1	35.25	8.19	
						6.100	15.82	10.24	128.1	0.6	35.27	8.17	2.9
						6.100	15.82	10.27	128.5	0.8	35.29	8.17	
						11.200	15.75	10.34	129.3	2.2	35.32	8.16	6.0
11.200	15.75	10.43	130.4	2.2	35.32	8.16							
2014/2/22 18:00	C1	ME	833708	808180	15.7	1.000	15.91	10.65	133.4	0.2	35.17	8.26	2.4
						1.000	15.91	10.61	132.9	0.3	35.22	8.25	
						7.850	15.9	10.54	132	0.2	35.27	8.23	3.3
						7.850	15.9	10.54	132.1	0.2	35.28	8.23	
						14.700	15.89	10.47	131.2	0.2	35.31	8.21	
14.700	15.89	10.46	131.1	0.1	35.33	8.21							
2014/2/22 17:04	C2	ME	831468	807716	10.1	1.000	15.8	10.72	133.8	1.2	35.01	8.08	2.6
						1.000	15.8	10.72	133.9	1.2	35.04	8.09	
						5.050	15.8	10.67	133.4	1.1	35.2	8.11	4.5
						5.050	15.81	10.68	133.6	1	35.2	8.11	
						9.100	15.8	10.74	134.4	1.1	35.26	8.12	
9.100	15.8	10.75	134.4	1	35.3	8.12							
2014/2/22 18:23	C3	ME	832224	808879	16.3	1.000	15.9	10.47	131.3	0.4	35.38	8.17	4.4
						1.000	15.9	10.61	133.1	0.3	35.36	8.18	
						8.150	15.88	10.6	132.8	0.1	35.38	8.17	2.4
						8.150	15.88	10.59	132.7	0.1	35.38	8.17	
						15.300	15.88	10.62	133.1	0.5	35.35	8.17	
15.300	15.88	10.65	133.4	0.3	35.33	8.17							
2014/2/22 10:43	W1	MF	832982	907708	2.7	1.350	15.82	11.69	145.5	0.8	34.46	8.04	2.5
1.350	15.83	11.67	145.3	0.7	34.48	8.05							
2014/2/22 10:52	W2	MF	832675	807996	12.2	1.000	15.81	12.98	161.6	0.7	34.56	8.11	2.9
						1.000	15.81	12.98	161.7	0.6	34.56	8.12	
						5.600	15.81	12.8	159.4	0.5	34.57	8.14	2.8
						6.100	15.81	12.8	159.4	0.5	34.57	8.14	
						11.200	15.8	12.68	157.9	2.7	34.57	8.14	
11.200	15.8	12.65	157.6	2.1	34.57	8.14							
2014/2/22 11:15	W3	MF	832024	807896	11.2	1.000	15.72	11.11	138.3	1	34.75	8.18	3.0
						1.000	15.72	11.07	137.8	0.9	34.76	8.18	
						5.600	15.7	11.05	137.5	0.7	34.76	8.18	2.6
						5.600	15.7	11.03	137.3	0.7	34.77	8.19	
						10.200	15.64	10.93	135.8	3.2	34.76	8.18	
10.200	15.64	10.9	135.5	6.9	34.77	8.18							
2014/2/22 10:28	C1	MF	833708	808180	15.3	1.000	15.78	11.44	142.1	0.4	34.27	8.03	2.7
						1.000	15.78	11.44	142.1	0.4	34.27	8.03	
						7.650	15.78	11.47	142.5	0.4	34.3	8.04	3.1
						7.650	15.78	11.48	142.6	0.4	34.3	8.03	
						14.300	15.77	11.48	142.7	0.6	34.31	8.04	
14.300	15.77	11.5	142.9	0.4	34.31	8.04							
2014/2/22 11:28	C2	MF	831468	807716	9.6	1.000	15.71	10.94	136.1	2.1	34.7	8.18	3.2
						1.000	15.71	11.01	137	1.8	34.71	8.18	
						4.800	15.71	10.9	135.6	0.8	34.69	8.18	2.6
						4.800	15.71	10.9	135.6	0.7	34.68	8.18	
						8.600	15.7	10.87	135.2	0.8	34.7	8.19	
8.600	15.71	10.86	135	1.2	34.68	8.19							
2014/2/22 10:03	C3	MF	832224	807879	15.8	1.000	15.77	11.41	141.5	0.3	34.01	7.99	2.1
						1.000	15.77	11.4	141.5	0.3	34.02	8	
						7.900	15.77	12.43	154.3	0.5	34.15	8.01	2.1
						7.900	15.77	12.29	152.5	0.5	34.15	8.01	
						14.800	15.77	12.94	160.6	0.4	34.18	8.02	
14.800	15.77	13.02	161.6	0.4	34.18	8.02							

MF- Mid Flood Tide

ME- Mid Ebb tide

Contract No. DC/2009/13

**Construction of Sewage Treatment Works  
at Yung Shue Wan and Sok Kwu Wan**



**Sok Kwu Wan**

Date 24-Feb-14

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2014/2/24 8:50	W1	ME	832981	807713	2.7	1.350	16.07	11.6	145.4	0.3	34.72	8.24	2.7
						1.350	16.07	11.61	145.4	0.2	34.72	8.24	
2014/2/24 8:58	W2	ME	832693	807985	13.4	1.000	16.07	11.73	147	0.8	34.69	8.21	2.6
						1.000	16.07	11.77	147.5	0.5	34.69	8.21	
						6.700	16.07	11.93	149.5	0.6	34.69	8.19	2.8
						6.700	16.07	11.97	149.9	0.4	34.69	8.19	
						12.400	16.07	12.06	151.1	2.6	34.71	8.18	
						12.400	16.07	12.05	151	1.6	34.72	8.18	
2014/2/24 9:17	W3	ME	832026	807904	11.8	1.000	16.16	10.09	126.8	0.3	34.89	8.09	4.3
						1.000	16.16	10.09	126.8	0.4	34.91	8.09	
						5.900	16.15	10.1	127	0.2	34.98	8.09	2.9
						5.900	16.16	10.05	126.4	0.2	35	8.09	
						10.800	16.14	10.32	129.8	0.4	35.02	8.09	
						10.800	16.14	10.19	128.2	0.5	35.05	8.09	
						10.800	16.14	10.19	128.2	0.5	35.05	8.09	
2014/2/24 8:38	C1	ME	833718	808165	15.6	1.000	16.03	11.38	142.2	0.2	34.39	8.05	2.2
						1.000	16.03	11.37	142.1	0.2	34.39	8.06	
						7.800	15.99	11.34	141.6	0.1	34.4	8.06	3.2
						7.800	15.99	11.33	141.5	0.1	34.4	8.06	
						14.600	15.91	11.34	141.4	0.1	34.38	8.06	
						14.600	15.9	11.34	141.3	0.1	34.39	8.06	
2014/2/24 9:45	C2	ME	831459	807716	9.7	1.000	16.18	9.77	122.9	0.5	35.04	8.1	2.6
						1.000	16.18	10.15	127.7	0.5	35.06	8.1	
						4.850	16.18	10.15	127.7	0.4	35.09	8.11	3.2
						4.850	16.18	10.17	128	0.4	35.08	8.11	
						8.700	16.16	10.28	129.4	0.4	35.1	8.11	
						8.700	16.16	10.31	129.7	0.4	35.1	8.11	
2014/2/24 8:20	C3	ME	832246	808878	15.4	1.000	16.04	11.55	144.1	0.2	34.18	8.01	3.1
						1.000	16.04	11.58	144.6	0.2	34.14	8.01	
						7.700	16.01	11.77	146.9	0.3	34.23	8.03	2.3
						7.700	15.99	11.76	146.7	0.2	34.26	8.03	
						14.400	15.91	11.7	145.8	2.9	34.32	8.04	
						14.400	15.9	11.61	144.7	2.1	34.34	8.05	
						14.400	15.9	11.61	144.7	2.1	34.34	8.05	
2014/2/24 12:56	W1	MF	832977	807725	2.8	1.400	16.38	9.68	122.7	1.2	35.62	8.08	4.5
2014/2/24 13:06	W2	MF	832693	807986	13.7	1.400	16.34	10.06	127.4	1.1	35.66	8.08	3.6
						1.000	16.26	9.74	122.9	2	35.31	7.97	
						1.000	16.26	9.88	124.7	1.7	35.35	7.96	3.6
						6.100	16.24	10.19	128.8	0.4	35.6	7.93	
						6.850	16.21	10.27	129.8	0.3	35.66	7.91	
						12.700	15.81	10.35	129.8	1.4	35.75	7.88	
12.700	15.81	10.32	129.5	1.1	35.76	7.87	3.2						
2014/2/24 13:25	W3	MF	832022	807893	12.2	1.000	16.34	10.58	133.9	0.4	35.57	7.89	4.3
						1.000	16.34	10.69	135.4	0.3	35.63	7.88	
						6.100	16.24	10.77	136.3	0.6	35.74	7.85	3.1
						6.100	16.23	10.73	135.8	0.7	35.75	7.85	
						11.200	16.2	11.49	145.3	1.8	35.77	7.84	
						11.200	16.2	10.61	134.1	1.8	35.77	7.84	
						11.200	16.2	10.61	134.1	1.8	35.77	7.84	
2014/2/24 12:43	C1	MF	833706	808179	17.1	1.000	16.06	11.22	141.3	0.1	35.6	7.93	2.7
						1.000	16.09	11.22	141.4	0.1	35.6	7.93	
						8.550	15.79	11.33	141.9	0.1	35.61	7.92	4.4
						8.550	15.7	11.21	140.3	0.2	35.64	7.91	
						16.100	15.7	11.2	140.2	0.2	35.64	7.91	
						16.100	15.69	10.96	137	0.4	35.64	7.91	
2014/2/24 13:40	C2	MF	831454	807716	9.4	1.000	16.44	11.35	144.2	0.4	35.72	7.87	3.7
						1.000	16.43	11.35	144.1	0.4	35.73	7.86	
						4.700	16.41	11.04	140.1	0.4	35.75	7.84	2.1
						4.700	16.4	10.95	139	0.3	35.76	7.84	
						8.400	16.33	10.92	138.4	0.5	35.76	7.84	
						8.400	16.34	10.92	138.4	0.4	35.75	7.83	
2014/2/24 12:20	C3	MF	832228	808879	16.8	1.000	16.1	11.49	144.9	0.1	35.59	8	2.0
						1.000	16.13	11.46	144.5	0.1	35.59	8	
						8.400	15.71	11.25	140.7	0.2	35.59	7.94	3.4
						8.400	15.71	11.25	140.7	0.3	35.6	7.94	
						15.800	15.7	11.13	139.2	0.1	35.61	7.92	
						15.800	15.7	11.13	139.2	0.1	35.61	7.92	
						15.800	15.7	11.13	139.2	0.1	35.61	7.92	


MF- Mid Flood Tide  
ME- Mid Ebb tide

## **Appendix I**


### **Graphical Plots of Monitoring Results**





### Air Quality Monitoring – 1 hour TSP Monitoring


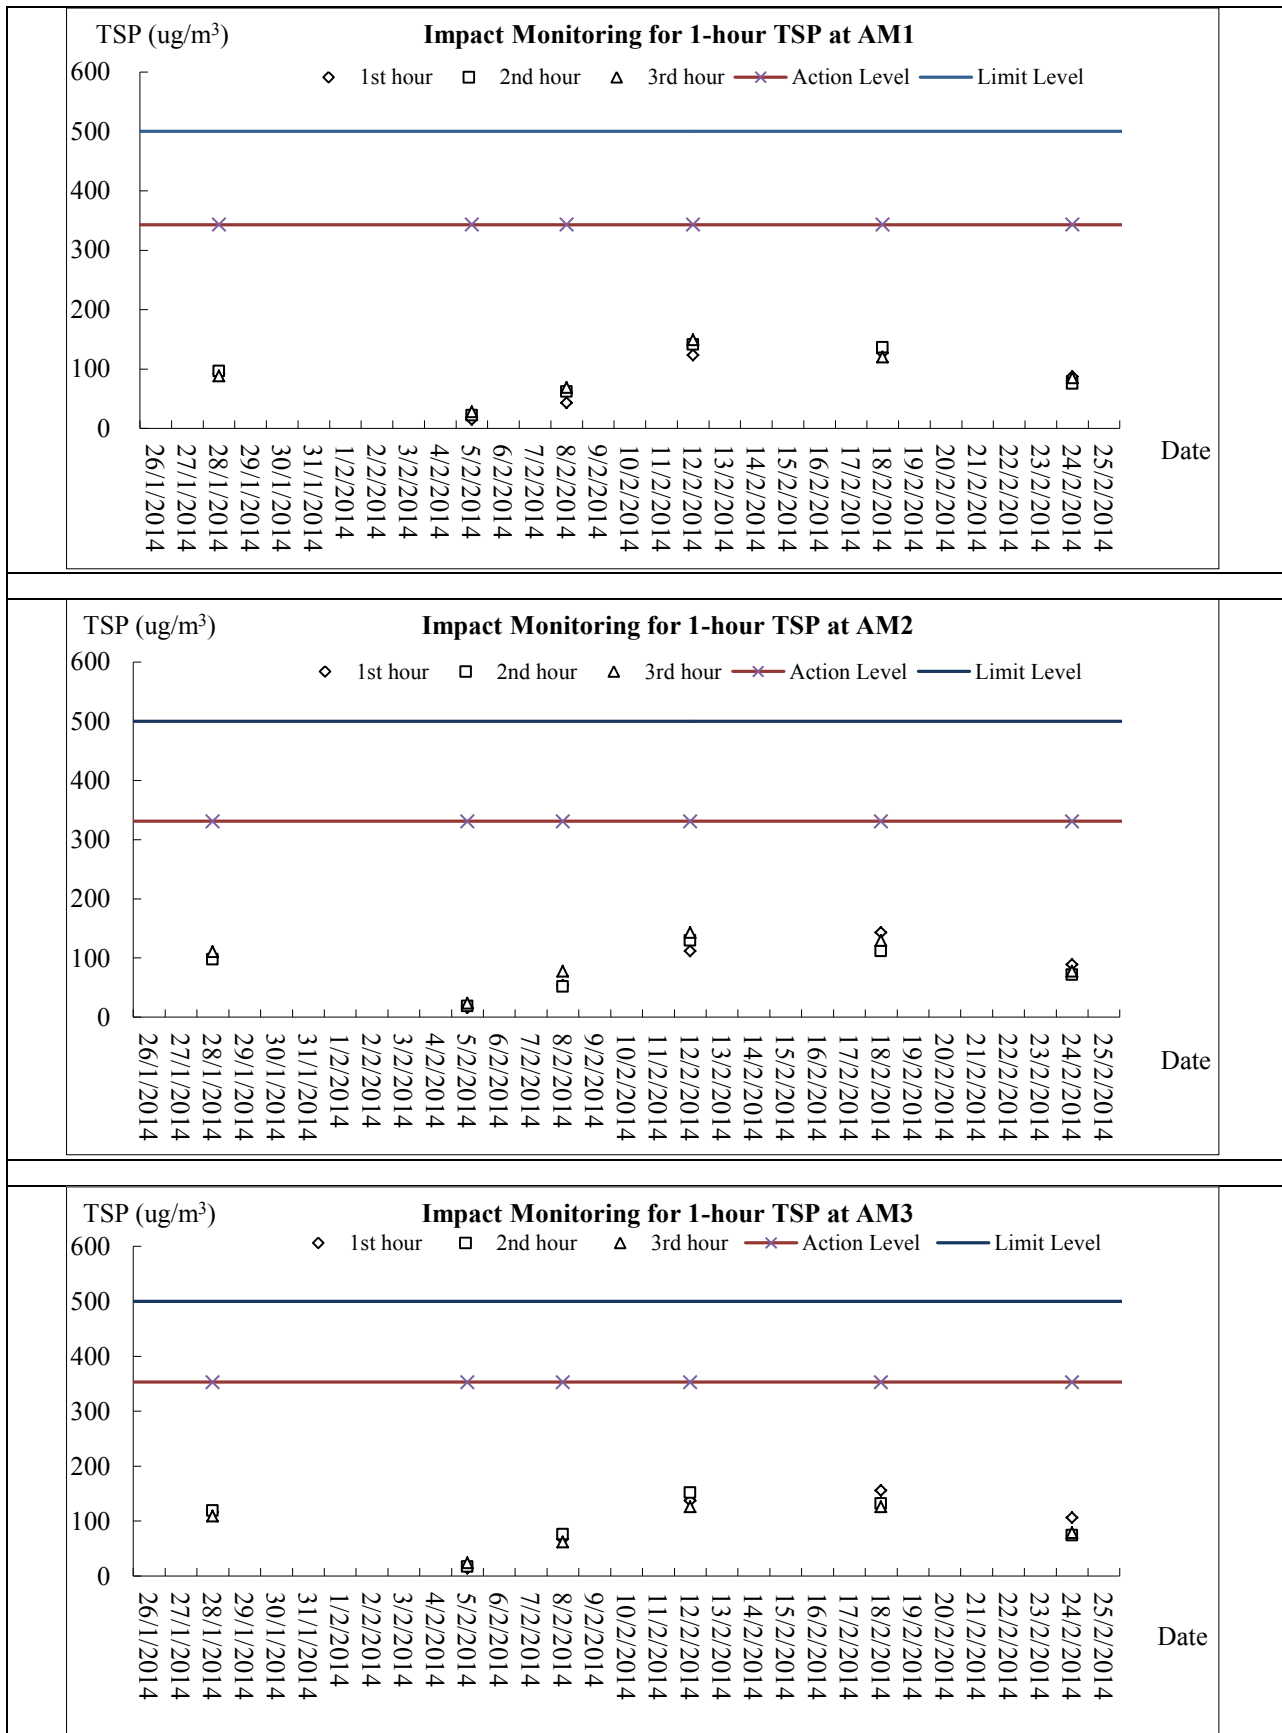


### Air Quality Monitoring – 24 hour TSP Monitoring


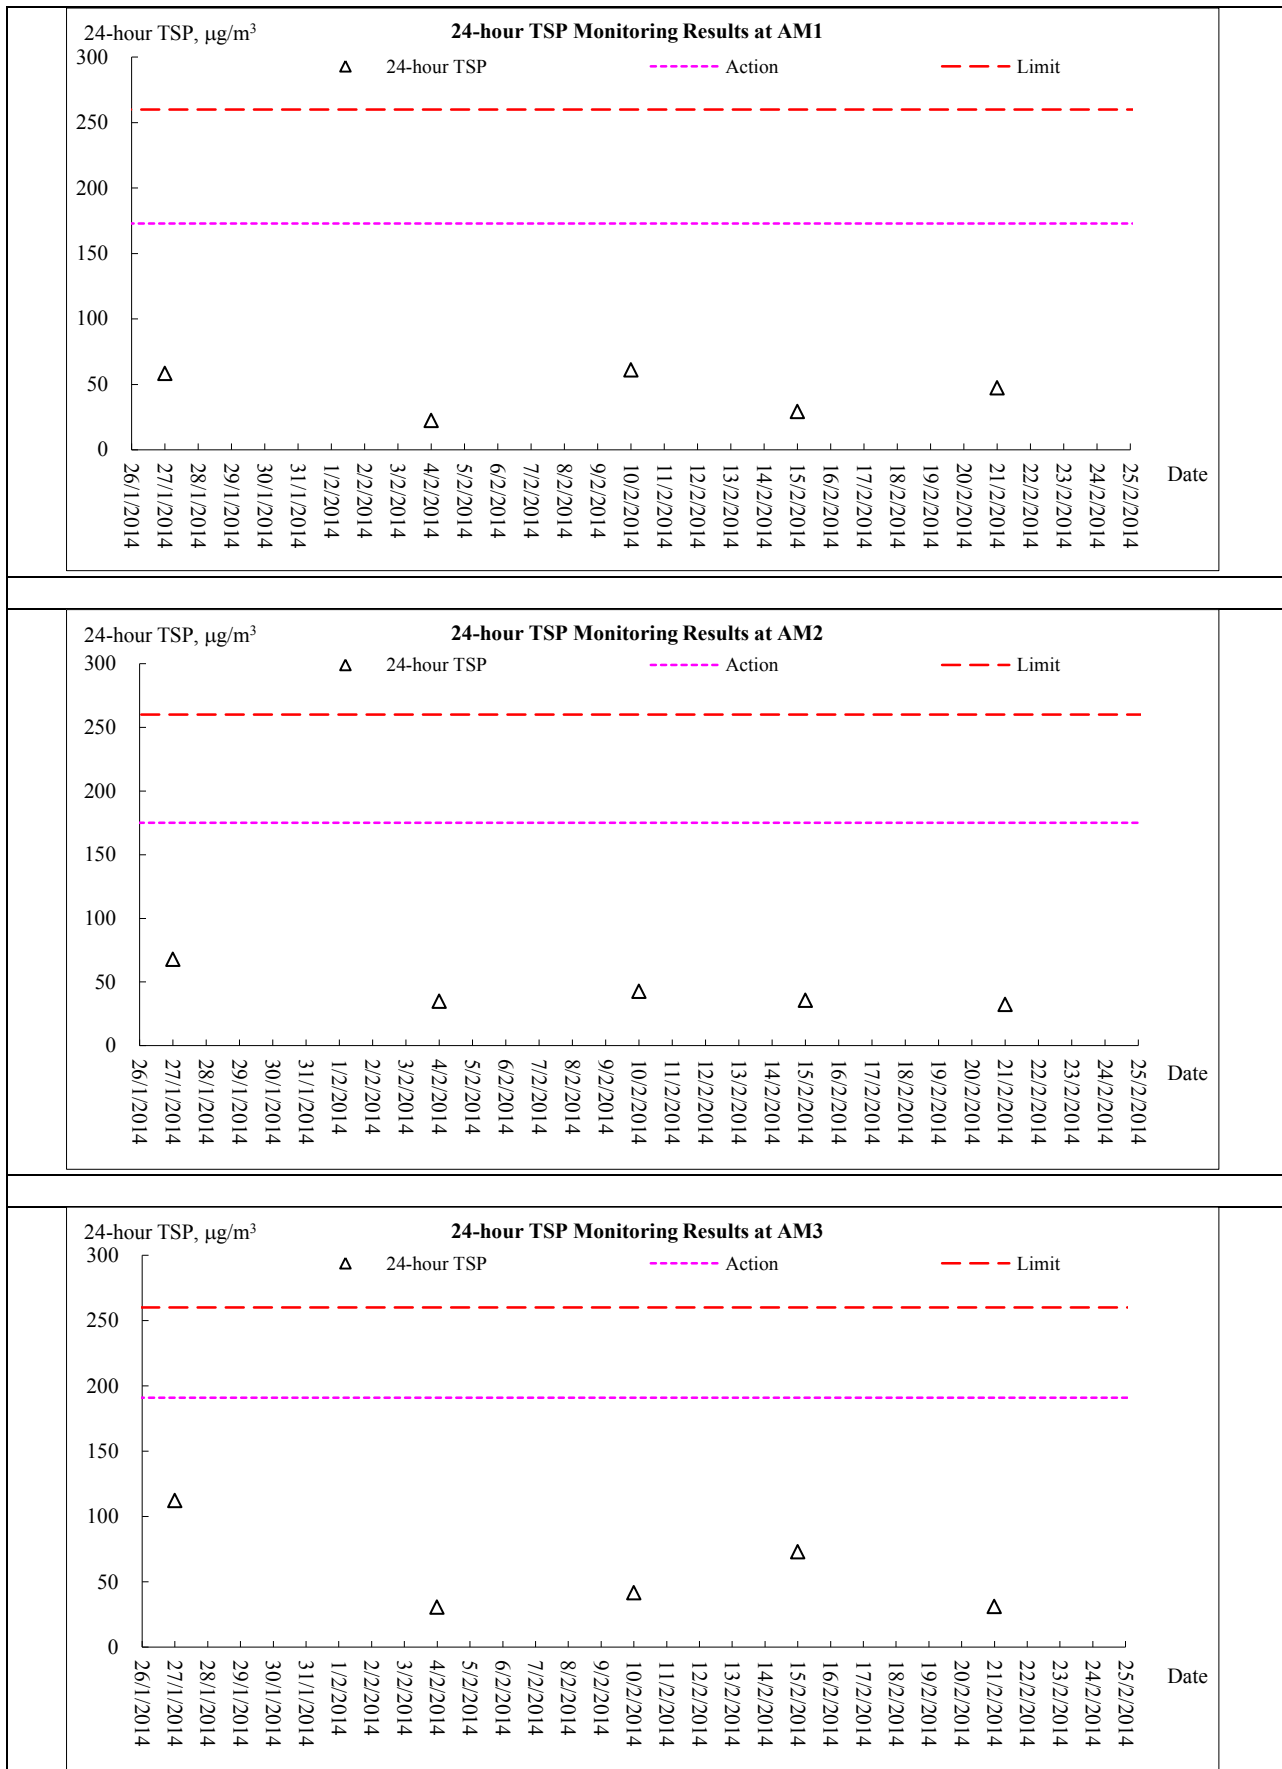




### Construction Noise Monitoring

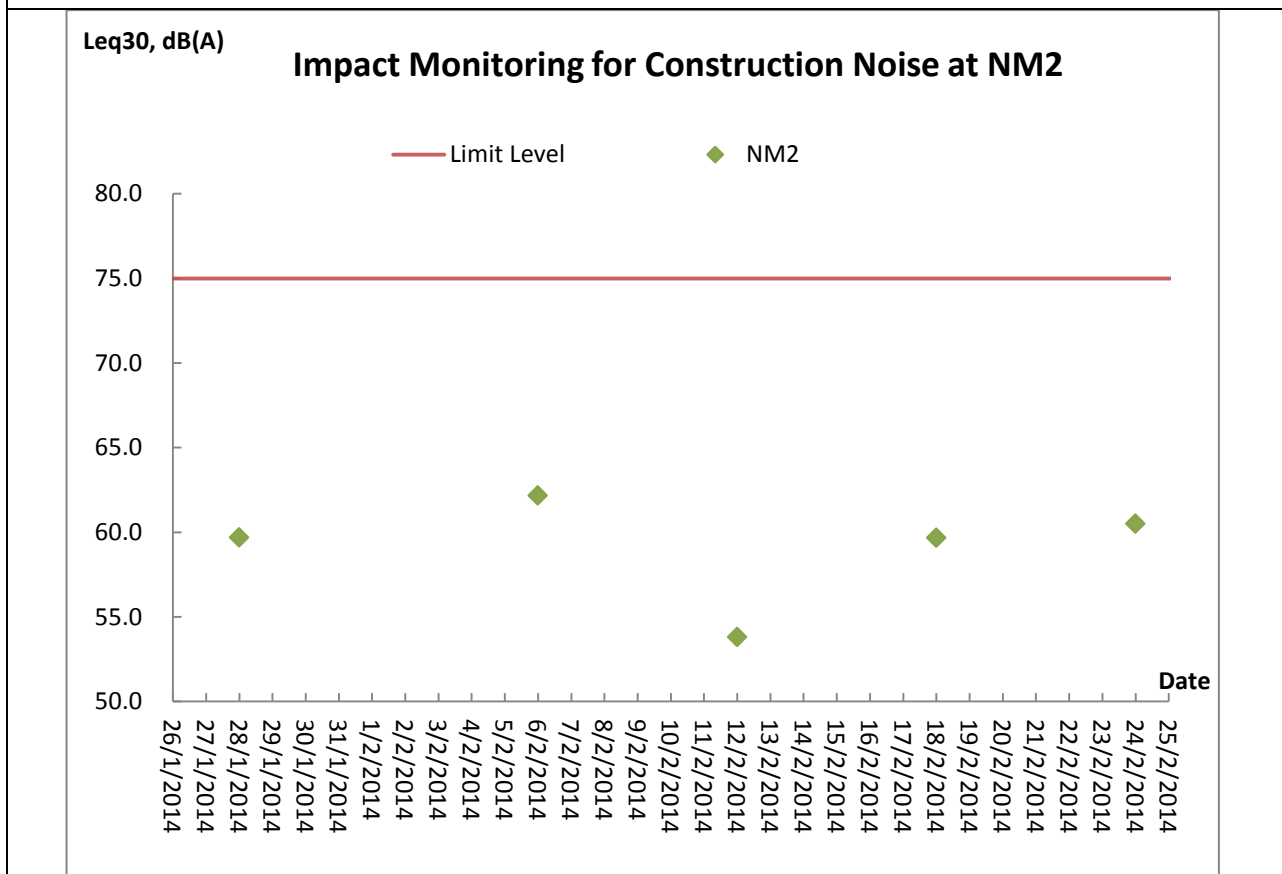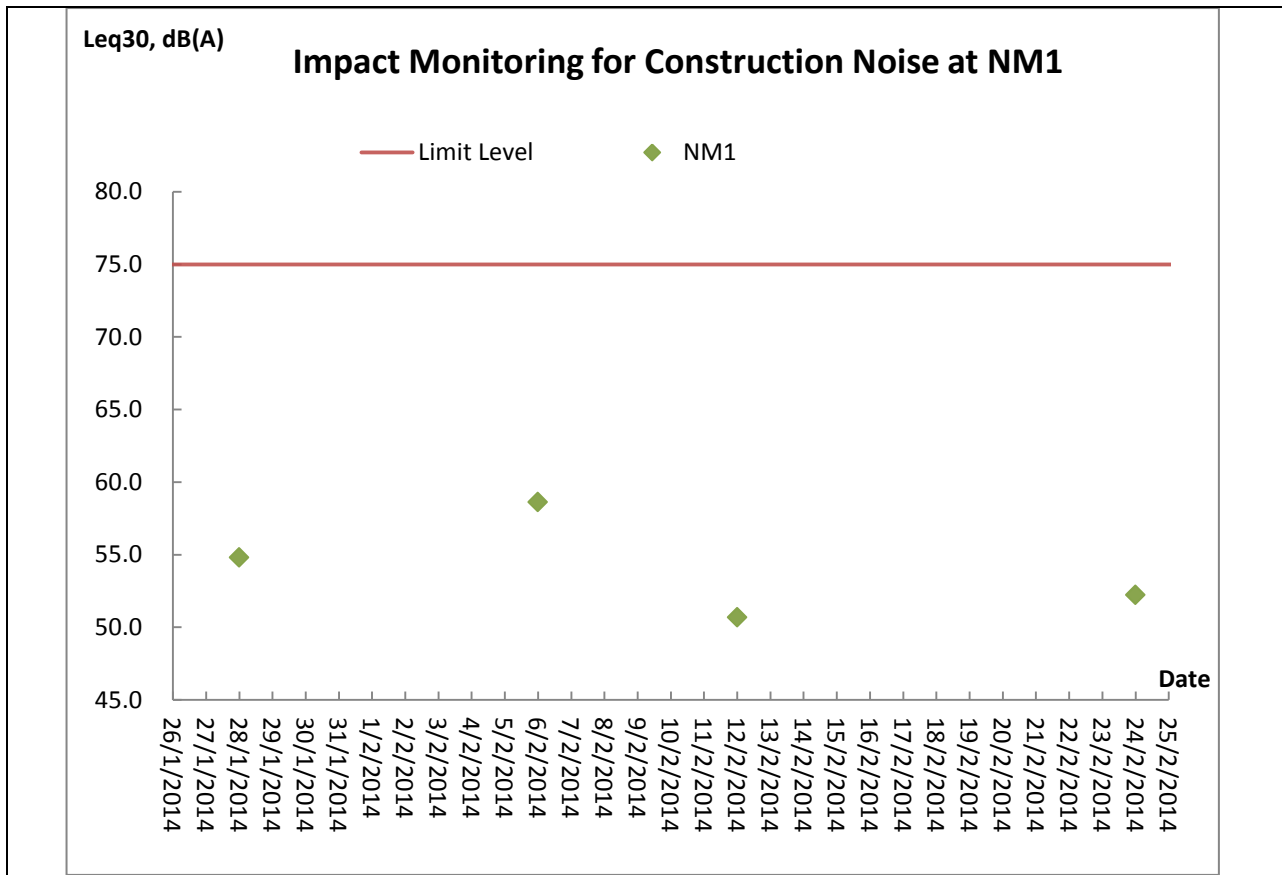

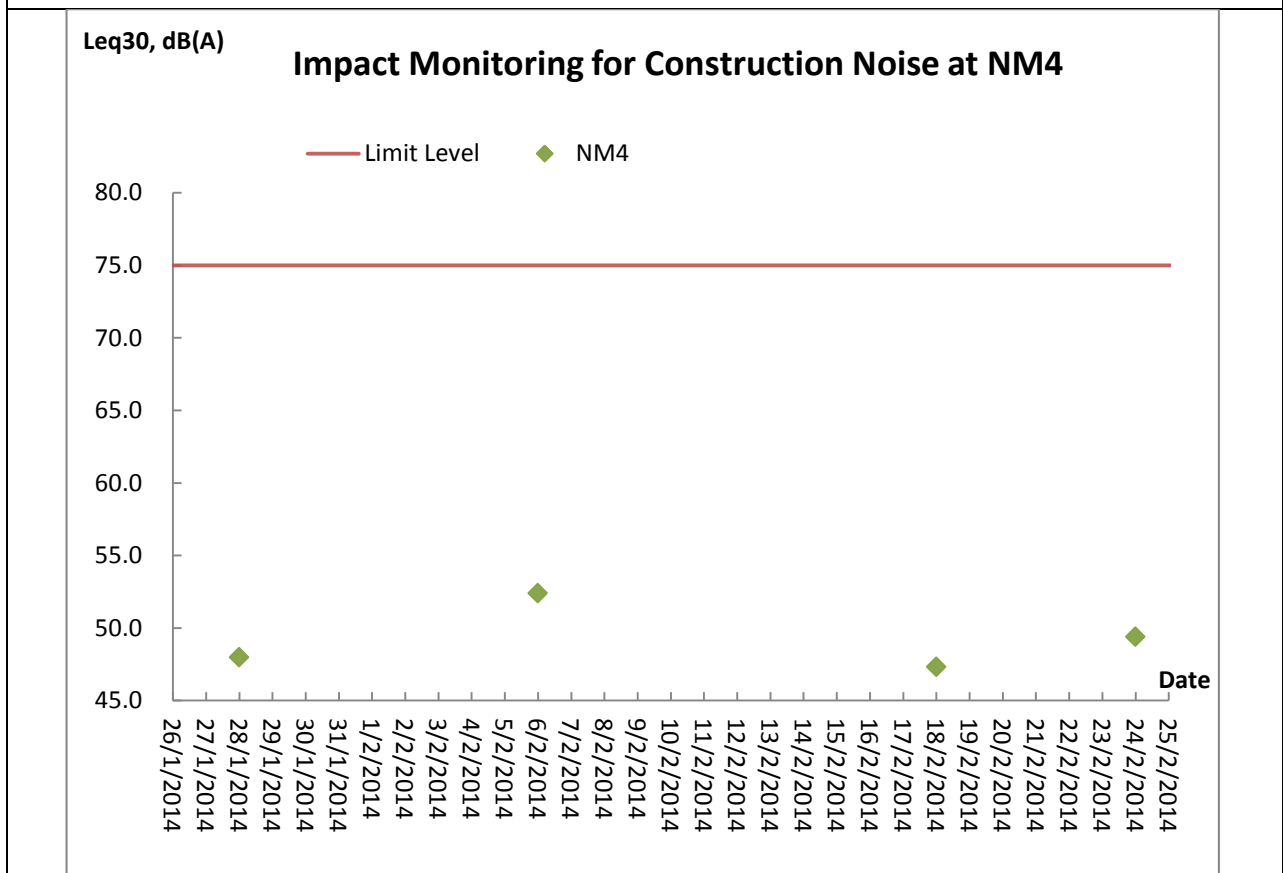
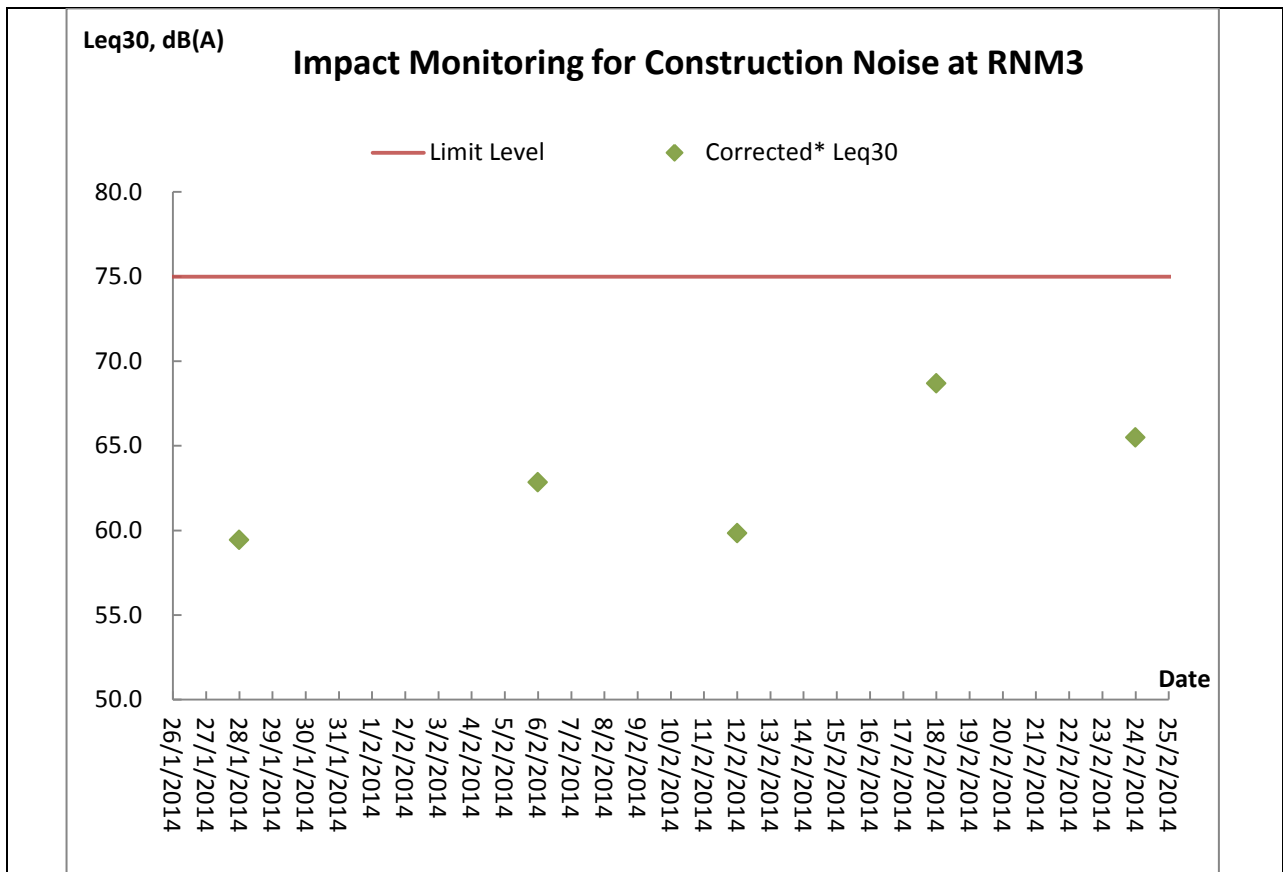




### Marine Water Quality Monitoring - Mid-Ebb Tide

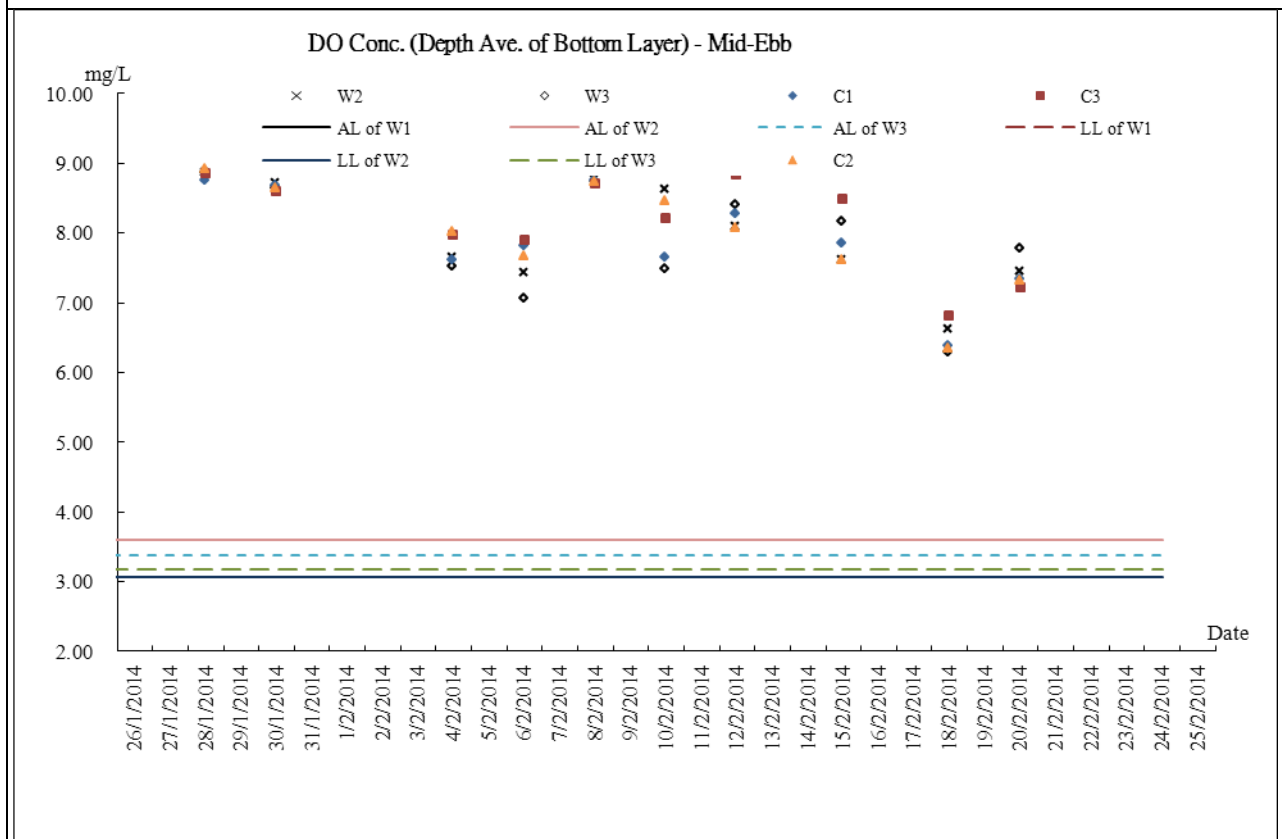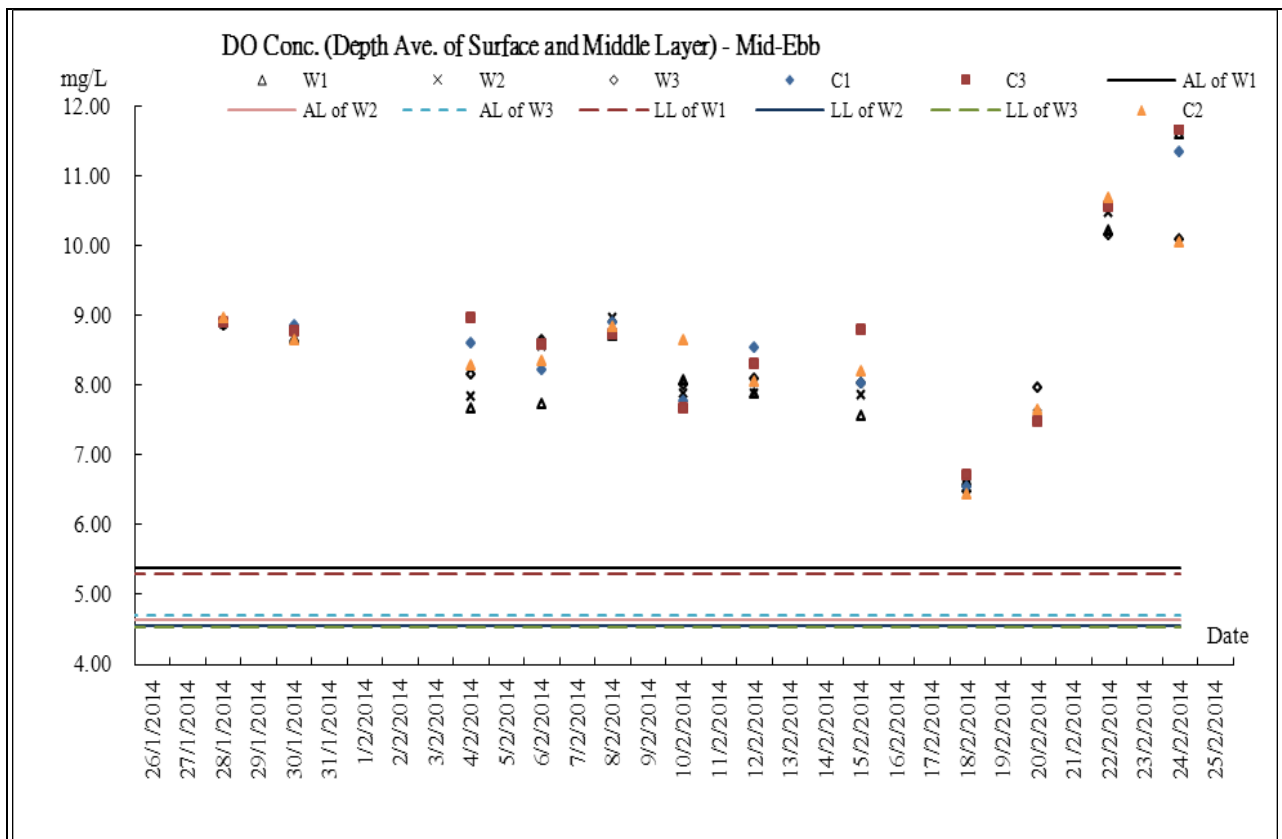

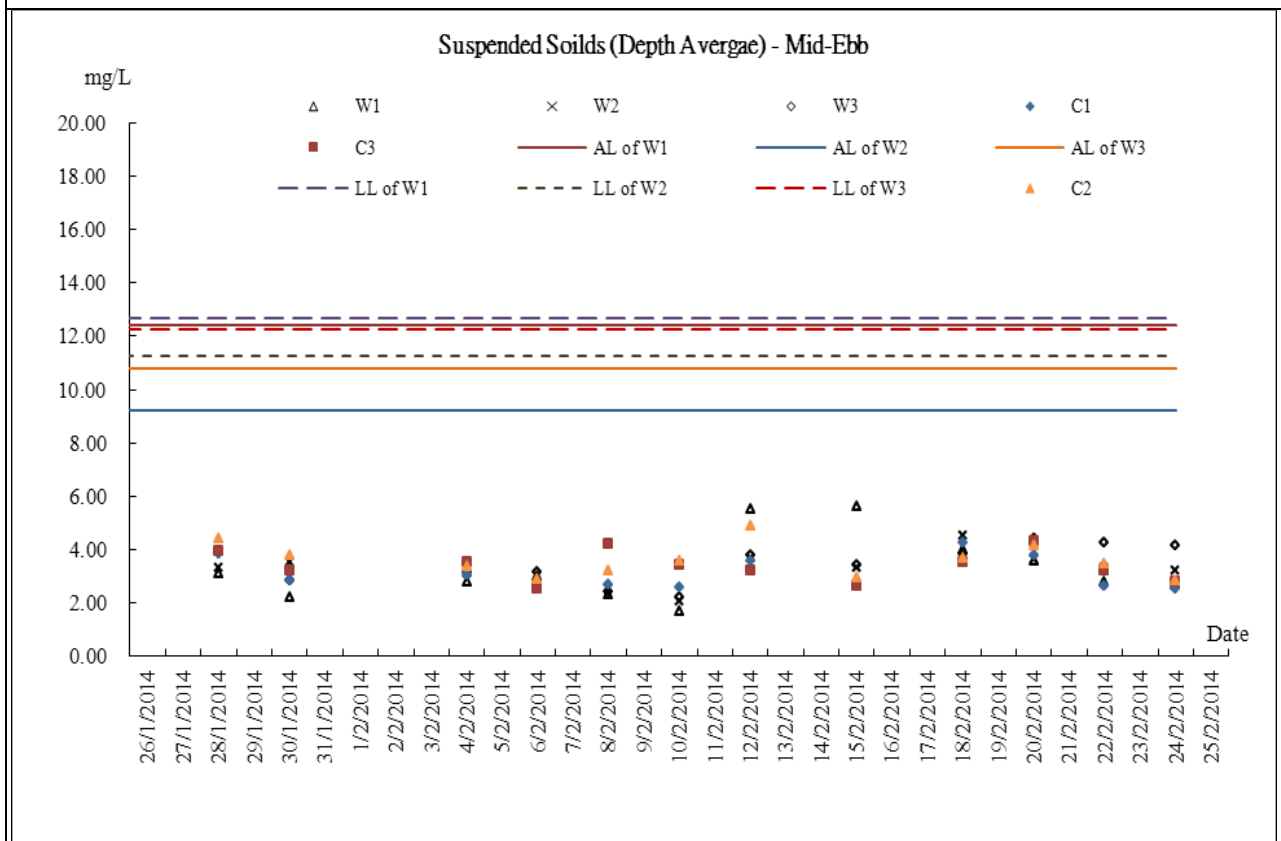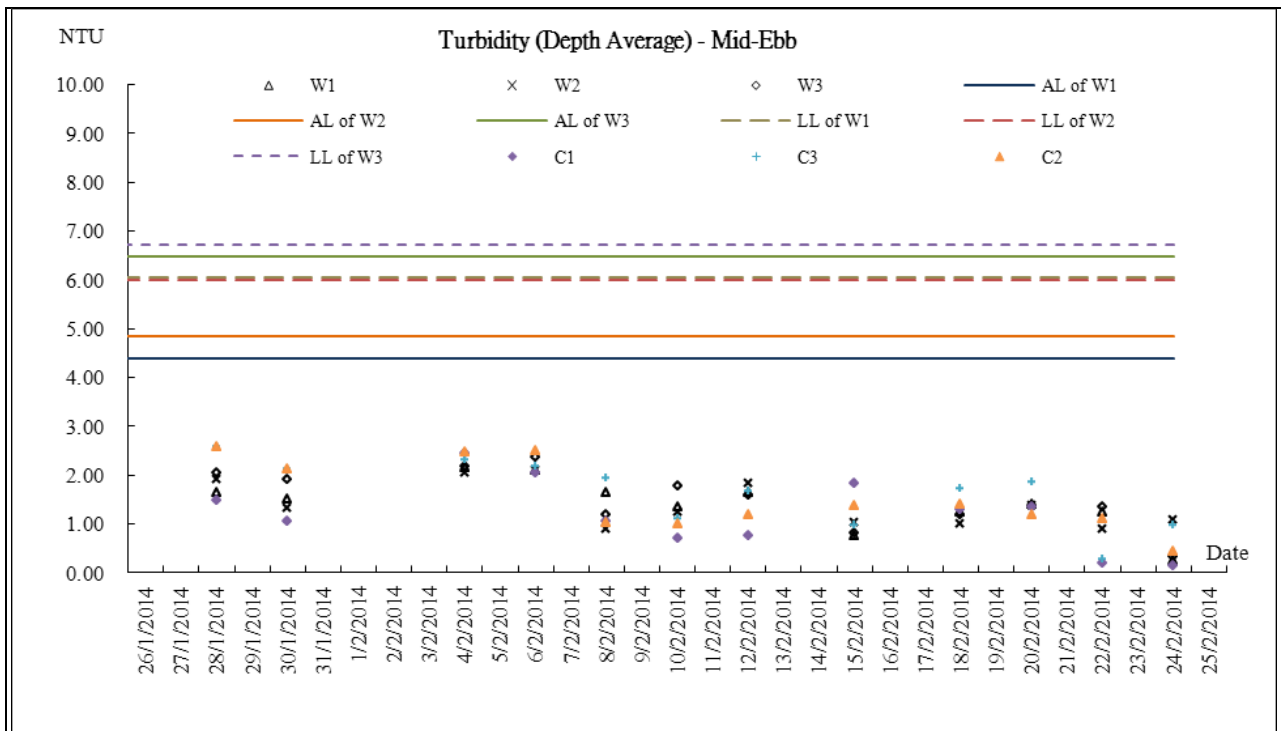

### Marine Water Quality Monitoring - Mid-Flood Tide

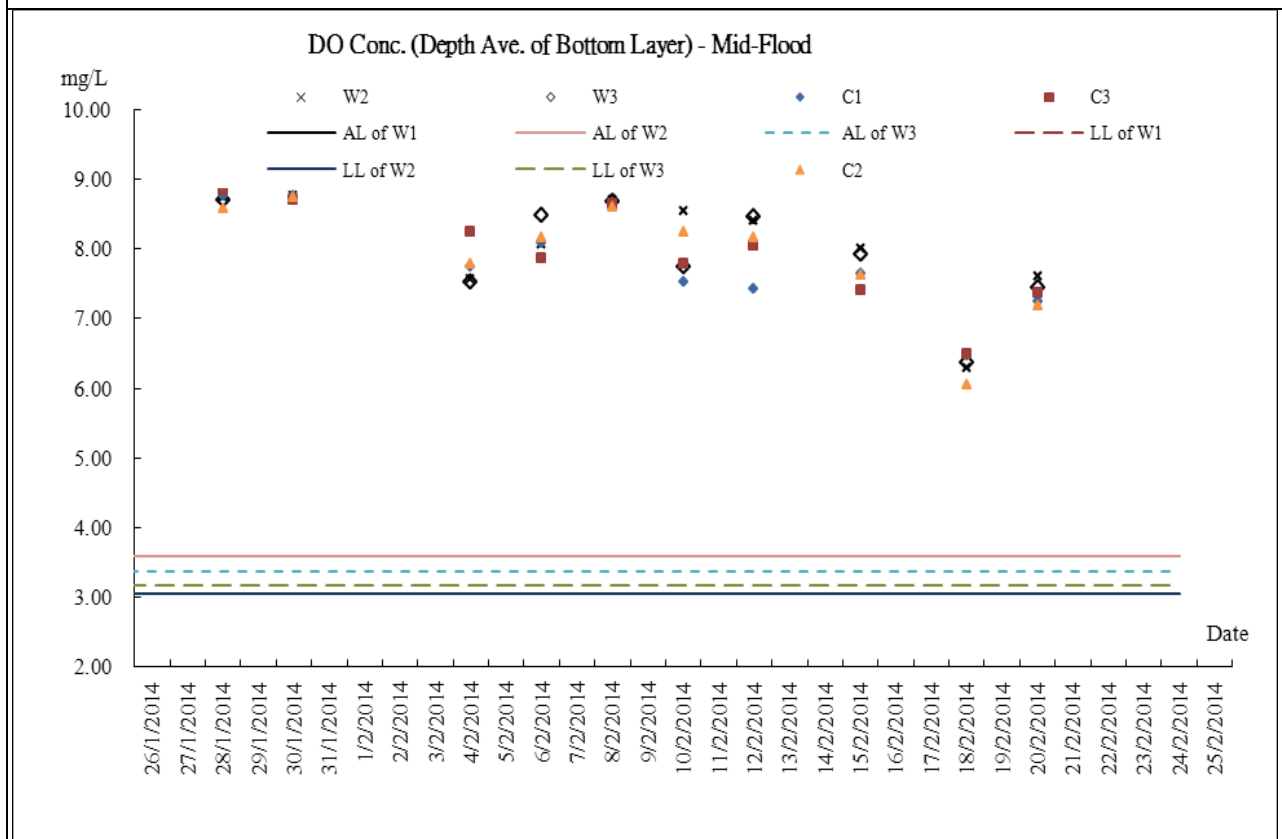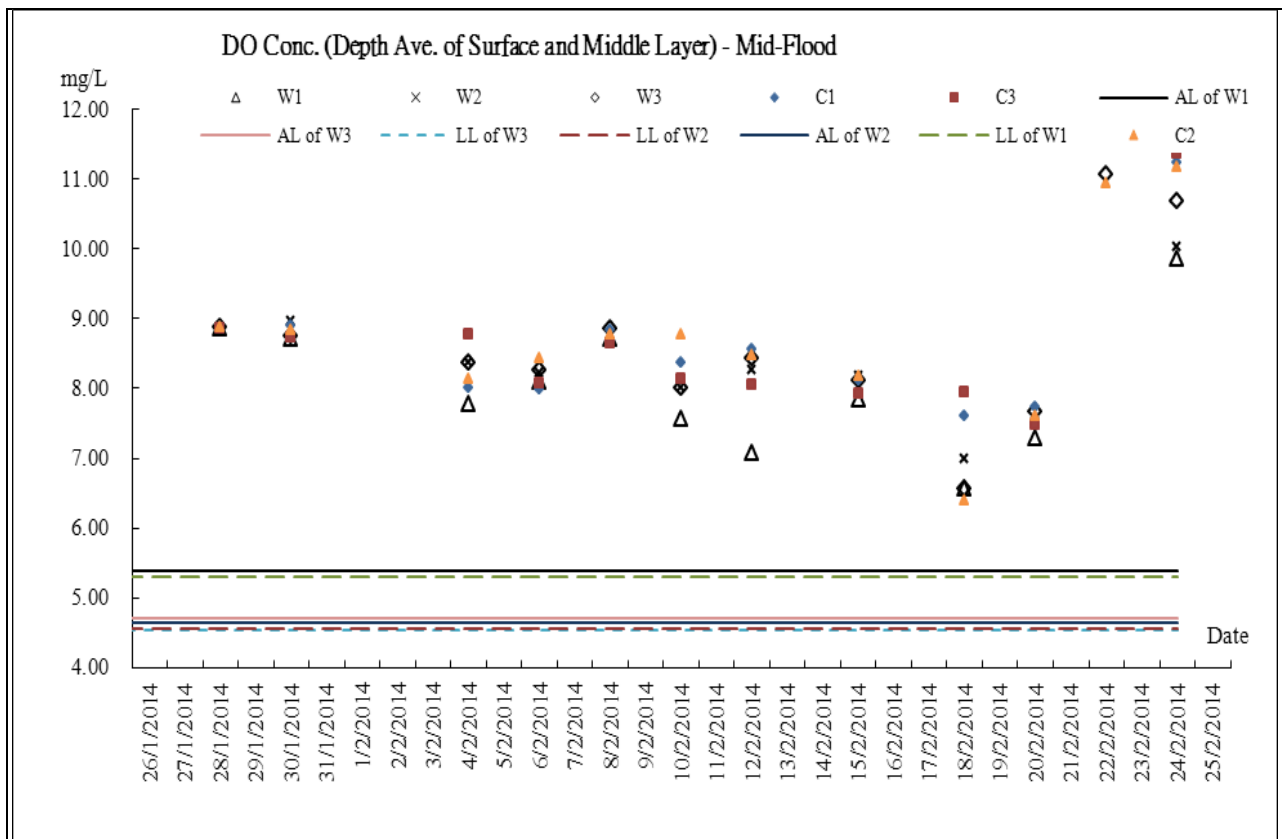

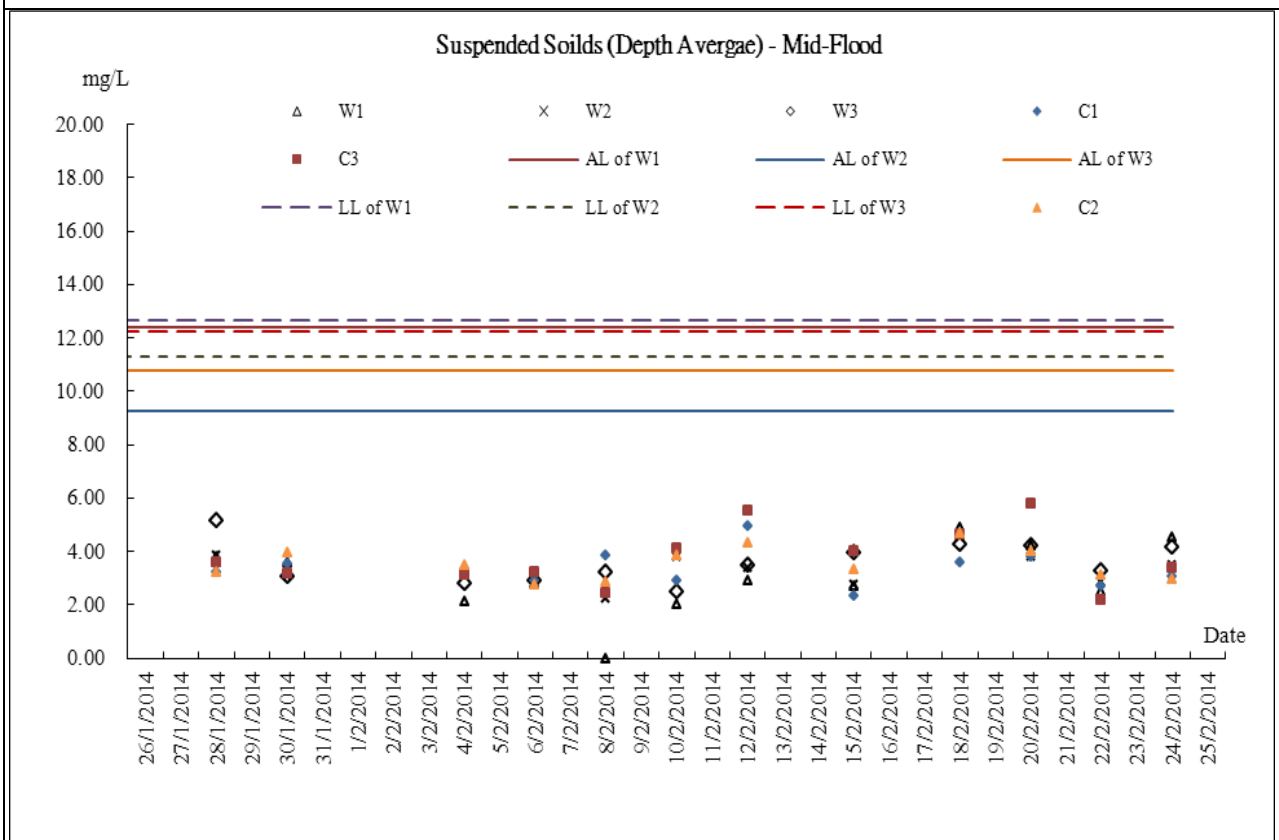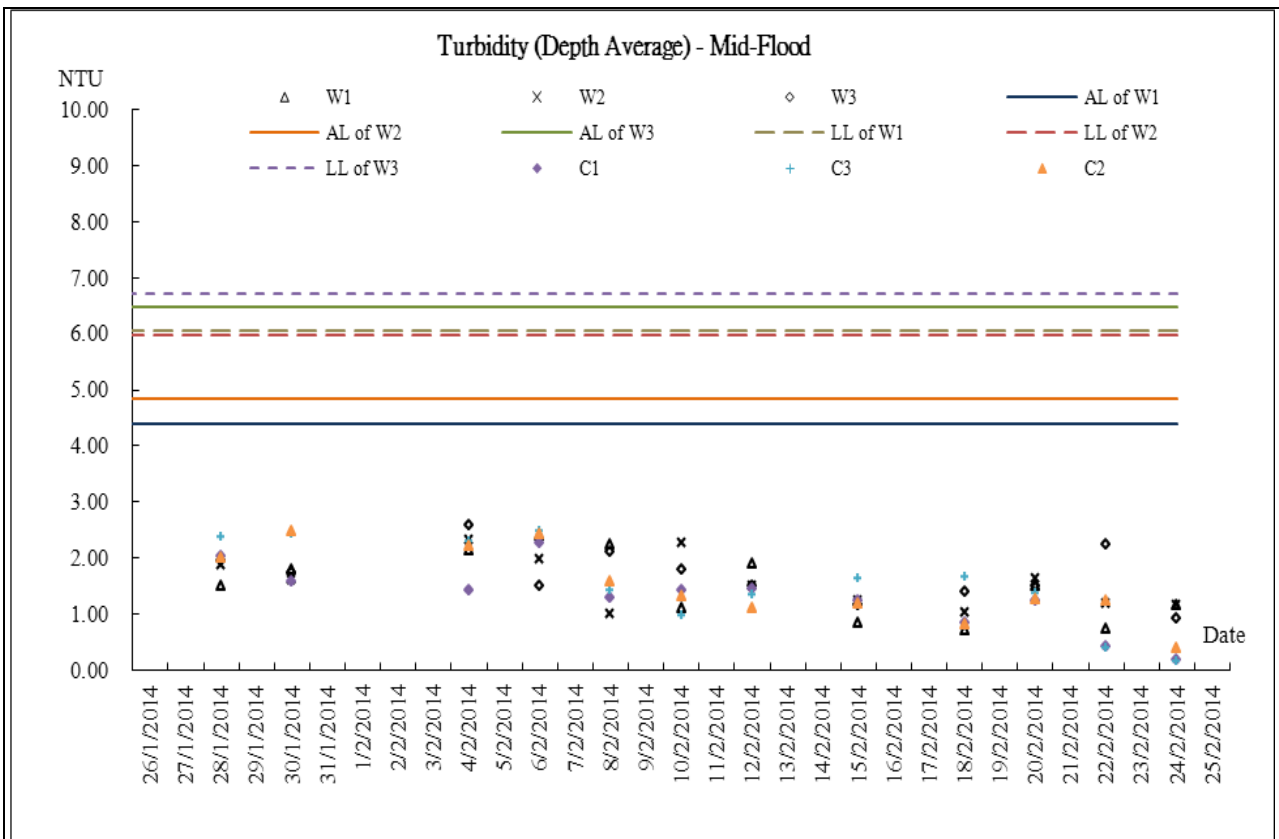



## **Appendix J**

### **Meteorological Information**

**Meteorological Data Extracted from HKO during the Reporting Period**

Date		Weather
25-Jan-14	Sat	Mainly fine and dry. Moderate easterly winds.
26-Jan-14	Sun	Mainly cloudy with sunny periods. Moderate easterly winds.
27-Jan-14	Mon	Mainly fine and dry. Moderate easterly winds.
28-Jan-14	Tue	Mainly fine and dry. Moderate easterly winds.
29-Jan-14	Wed	Fine, dry. Moderate easterly winds, fresh at times.
30-Jan-14	Thu	Fine, dry. Light to moderate easterly winds.
31-Jan-14	Fri	Fine. Dry with some haze. Light to moderate easterly winds.
1-Feb-14	Sat	Warm with sunny periods during the day. Light to moderate east to southeasterly winds.
2-Feb-14	Sun	Warm with sunny periods during the day. Light to moderate east to southeasterly winds.
3-Feb-14	Mon	Cloudy with a few rain patches. Fresh easterly winds, strong at times.
4-Feb-14	Tue	Cloudy. One or two rain patches later. Moderate to fresh easterly winds, strong at times.
5-Feb-14	Wed	Cloudy with one or two rain patches. Fresh easterly winds, strong at times.
6-Feb-14	Thu	Mainly cloudy. Sunny intervals in the afternoon. Moderate easterly winds.
7-Feb-14	Fri	Cloudy, mist, sunny periods. Light to moderate easterly winds.
8-Feb-14	Sat	Cold and cloudy with a few rain patches. Fresh northerly winds.
9-Feb-14	Sun	Cold and cloudy with a few rain patches. Fresh northerly winds.
10-Feb-14	Mon	Cold and cloudy with a few rain patches. Fresh northerly winds.
11-Feb-14	Tue	Cold, cloudy, rain. Moderate to fresh north to northeasterly winds.
12-Feb-14	Wed	Cold, cloudy to overcast with a few rain patches. Moderate northeasterly winds.
13-Feb-14	Thu	Cloudy, very cold. Moderate to fresh north to northeasterly winds
14-Feb-14	Fri	Dry, sunny periods, Mainly cloudy, cold. Moderate to fresh north to northeasterly winds.
15-Feb-14	Sat	Dry, sunny periods, Mainly cloudy, cold. Moderate to fresh north to northeasterly winds.
16-Feb-14	Sun	Cloudy, very cold. Moderate to fresh north to northeasterly winds
17-Feb-14	Mon	Humid with fog. Sunny intervals at first. Moderate northerly winds.
18-Feb-14	Tue	Humid with fog. Sunny intervals at first. Moderate northerly winds.
19-Feb-14	Wed	Cloudy and cold. A few rain patches at first. Fresh to strong northerly winds.
20-Feb-14	Thu	Sunny periods, mainly cloudy. Fresh easterly winds, strong at times.
21-Feb-14	Fri	Sunny periods, mainly cloudy. Fresh easterly winds, strong at times.
22-Feb-14	Sat	Sunny periods, mainly cloudy. Fresh easterly winds, strong at times.
23-Feb-14	Sun	Mainly cloudy with a few light rain patches at first. Moderate easterly winds.
24-Feb-14	Mon	Mainly cloudy with a few light rain patches at first. Moderate easterly winds.
25-Feb-14	Tue	Mainly cloudy with a few light rain patches at first. Moderate easterly winds.

## **Appendix K**

### **Monthly Summary Waste Flow Table**

## Monthly Summary Waste Flow Table for February 2014

Month	Actual Quantities of Inert C&D Materials Generated Monthly												Actual Quantities of C&D Wastes Generated Monthly									
	Total Quantity Generated (a) = (c)+(d)+(e)		Hard Rock and Large Broken Concrete (b)		Reused in the Contract (c)		Reused in other Projects (d)		Disposed as Public Fill (e)		Imported Fill (f)		Metals		Paper/ cardboard packaging		Plastics		Chemical Waste		Others, e.g. rubbish	
	(in '000m <sup>3</sup> )		(in '000m <sup>3</sup> )		(in '000m <sup>3</sup> )		(in '000m <sup>3</sup> )		(in '000m <sup>3</sup> )		(in '000m <sup>3</sup> )		(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in tonne)	
	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW
<b>2014</b>	15.933	50.762	0.160	0.432	0.740	2.802	0.000	0.000	15.194	47.960	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	487.580	290.030
Jan	0.342	0.325	0.000	0.005	0.000	0.000	0.000	0.000	0.342	0.325	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	4.480	4.820
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	18.110	4.300
Mar																						
Apr																						
May																						
Jun																						
<b>Sub-total</b>	16.275	51.087	0.160	0.437	0.740	2.802	0.000	0.000	15.536	48.285	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	510.170	299.150
Jul																						
Aug																						
Sep																						
Oct																						
Nov																						
Dec																						
<b>Total</b>	16.275	51.087	0.160	0.437	0.740	2.802	0.000	0.000	15.536	48.285	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	510.170	299.150
	67.362		0.597		3.542		0.000		63.821		0.000		0.000		0.000		0.000		0.000		809.320	

Remark: Assume 1.0 m<sup>3</sup> vehicle dump load = 1.6 tonnes C&D materials

YSW: Yung Shue Wan

SKW: Sok Kwu Wan

## **Appendix L**

### **Weekly Site Inspection Checklist**

Project: TCS/00512/09  
DC-2009-13: Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan

Inspected by  
 ETL/ ET's Representative  
 RE's Representative  
 Contractor's Representative  
 IEC's Representative

Checklist No. TCS512B-28 Jan 2014  
 Mr. Martin Li  
 Mr. Daniel Chau  
 Mr. M.K. Leung

Date: 28 January 2014

Time: 11:00

**PART A: GENERAL INFORMATION**

Environmental Permit No.

Weather:  Sunny  Fine  Cloudy  Rainy  
 Temperature: 17.0 °C  
 Humidity:  High  Moderate  Low  
 Wind:  Strong  Breeze  Light  Calm

EP- 281/2007A

**Area Inspected**

1 Sok Kwu Wan

**PART B: SITE AUDIT**

Note:	Not Obs.:	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Note:</b> Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Section 1: Water Quality</b>						
1.01	Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02	Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03	Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04	Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07	Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08	As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.09	Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.10	Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12	Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13	Are wheel washing facilities well maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.14	Is runoff from wheel washing facilities avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.15	Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Are the vehicle and plant servicing areas paved and located within roofed areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.18	Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19	Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20	Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.21	Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.22	Are the oil interceptors/grease traps maintained properly?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.23	Is used bentonite recycled where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>Section 2: Air Quality</b>							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must be removed from the site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 3: Noise</b>							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 4: Waste/Chemical Management</b>							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.06	Are the chemical waste containers and storage area properly labelled?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.08	Is the chemical container or equipment provided with drip tray?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will be managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	




Note:	Not Obs.:	Yes:	No:	Follow Up:	N/A:	Photo/Remarks:
	Not Observed;	Compliance;	Non-Compliance;	Observations requiring follow-Up actions	N/A: Not Applicable	
<b>Section 5: Landscape &amp; Visual</b>						
5.01	Are retained and transplanted trees in health condition?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
5.02	Are retained and transplanted trees properly protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03	Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is damage to trees outside site boundary due to construction activities avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 6: Others</b>						
6.01	Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

(Sok Kwu Wan)


Remarks:

Findings of Site Inspection: (28 January 2014)

Follow up ( 28 January 2014 )

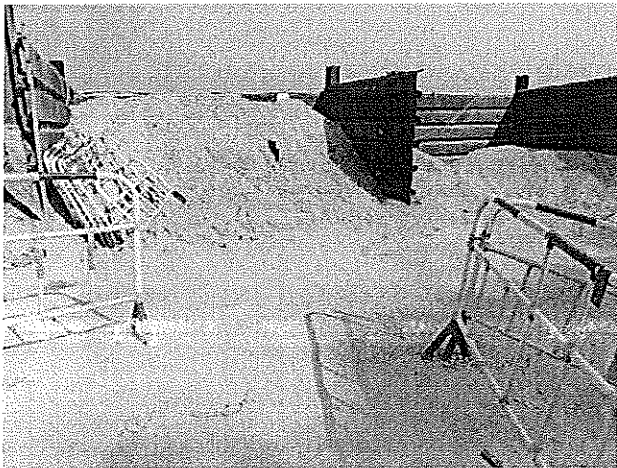

Stockpile of dusty materials without cover was observed, the Contractor was reminded to cover it with tarpaulin sheet to prevent dust disperse into air.

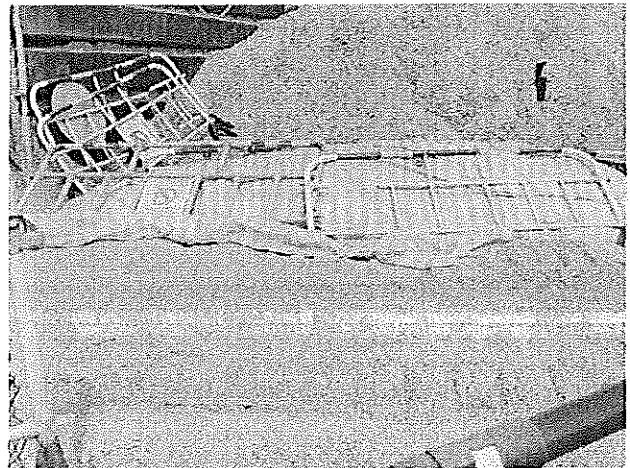

Stockpile of dusty material has been covered with tarpaulin sheet.

IEC's representative      RE's representative      ET's representative      EO's representative      Contractor's representative

( )      (Mr. Daniel Chau)      ( Mr. Martin Li )      ( Mr. M.K. Leung )      ( )

Project: TCS/00512/09  
DC-2009-13: Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan

Inspected by  
 ETL/ ET's Representative  
 RE's Representative  
 Contractor's Representative  
 IEC's Representative

Checklist No. TCS512B-6 Feb 2014  
 Mr. Martin Li  
 Mr. Daniel Chau  
 Mr. M.K. Leung

Date: 6 February 2014

Time: 11:00

**PART A: GENERAL INFORMATION**

Environmental Permit No.

Weather:  Sunny  Fine  Cloudy  Rainy  
 Temperature:  °C  
 Humidity:  High  Moderate  Low  
 Wind:  Strong  Breeze  Light  Calm

EP- 281/2007A

**Area Inspected**

1 Sok Kwu Wan

**PART B: SITE AUDIT**

Note:	Not Obs.:	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Note:</b> Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Section 1: Water Quality</b>						
1.01	Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02	Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03	Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04	Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07	Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08	As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.09	Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.10	Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12	Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13	Are wheel washing facilities well maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.14	Is runoff from wheel washing facilities avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.15	Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Are the vehicle and plant servicing areas paved and located within roofed areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.18	Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19	Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20	Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.21	Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.22	Are the oil interceptors/grease traps maintained properly?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.23	Is used bentonite recycled where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>Section 2: Air Quality</b>							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must be removed from the site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 3: Noise</b>							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 4: Waste/Chemical Management</b>							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.06	Are the chemical waste containers and storage area properly labelled?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.08	Is the chemical container or equipment provided with drip tray?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will be managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Section 5: Landscape &amp; Visual</b>							
5.01	Are retained and transplanted trees in health condition?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
5.02	Are retained and transplanted trees properly protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03	Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is damage to trees outside site boundary due to construction activities avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 6: Others</b>							
6.01	Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

(Sok Kwu Wan)

Remarks:

Findings of Site Inspection: (6 February 2014)

Follow up: ( 6 February 2014 )

No environmental issue was observed during the site inspection

Nil

IEC's representative      RE's representative      ET's representative      EO's representative      Contractor's representative

( )      (Mr. Daniel Chau)      ( Mr. Martin Li )      ( Mr. M.K. Leung)      ( )

Project: TCS/00512/09  
DC-2009-13: Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan

Inspected by  
 ETL/ ET's Representative  
 RE's Representative  
 Contractor's Representative  
 IEC's Representative

Checklist No. TCS512B-11 Feb 2014  
 Mr. Martin Li  
 Mr. Daniel Chau  
 Mr. M.K. Leung

Date: 11 February 2014

Time: 11:00

**PART A: GENERAL INFORMATION**

Environmental Permit No.

Weather:  Sunny  Fine  Cloudy  Rainy  
 Temperature:  °C  
 Humidity:  High  Moderate  Low  
 Wind:  Strong  Breeze  Light  Calm

EP- 281/2007A

**Area Inspected**

1 Sok Kwu Wan

**PART B: SITE AUDIT**

Note:	Not Obs.:	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Note:</b> Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Section 1: Water Quality</b>						
1.01	Is an effluent discharge license obtained for the Project?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02	Is the effluent discharged in accordance with the discharge licence?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03	Is the discharge of turbid water avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04	Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07	Is drainage system well maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08	As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.09	Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.10	Are earthworks final surfaces well compacted or protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Are manholes adequately covered or temporarily sealed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12	Are there any procedures and equipment for rainstorm protection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13	Are wheel washing facilities well maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.14	Is runoff from wheel washing facilities avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.15	Are there toilets provided on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are toilets properly maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Are the vehicle and plant servicing areas paved and located within roofed areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.18	Is the oil/grease leakage or spillage avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19	Are there any measures to prevent leaked oil from entering the drainage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20	Are there any measures to collect spilt cement and concrete washings during concreting works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.21	Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.22	Are the oil interceptors/grease traps maintained properly?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.23	Is used bentonite recycled where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>Section 2: Air Quality</b>							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must be removed from the site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 3: Noise</b>							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 4: Waste/Chemical Management</b>							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.06	Are the chemical waste containers and storage area properly labelled?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.08	Is the chemical container or equipment provided with drip tray?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will be managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	



Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Section 5: Landscape &amp; Visual</b>						
5.01 Are retained and transplanted trees in health condition?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
5.02 Are retained and transplanted trees properly protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03 Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04 Is damage to trees outside site boundary due to construction activities avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05 Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 6: Others</b>						
6.01 Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

(Sok Kwu Wan)




Remarks:

Findings of Site Inspection: (11 February 2014)

Follow up ( 11 February 2014 )

No environmental issue was observed during the site inspection

Nil.

<u>IEC's representative</u>	<u>RE's representative</u>	<u>ET's representative</u>	<u>EO's representative</u>	<u>Contractor's representative</u>
( )	 (Mr. Daniel Chau)	 ( Mr. Martin Li )	 ( Mr. M.K. Leung)	( )

Project: TCS/00512/09  
DC-2009-13: Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan

Inspected by  
 ETL/ ET's Representative  
 RE's Representative  
 Contractor's Representative  
 IEC's Representative

Checklist No. TCS512B-18 Feb 2014  
 Mr. Martin Li  
 Mr. Daniel Chau  
 Mr. M.K. Leung

Date: 18 February 2014

Time: 11:00

**PART A: GENERAL INFORMATION**

Environmental Permit No.

Weather:  Sunny  Fine  Cloudy  Rainy  
 Temperature:  °C  
 Humidity:  High  Moderate  Low  
 Wind:  Strong  Breeze  Light  Calm

EP- 281/2007A

**Area Inspected**

1 Sok Kwu Wan

**PART B: SITE AUDIT**

Note:	Not Obs.:	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Note:</b>	Not Obs.: Not Observed; <b>Yes:</b> Compliance; <b>No:</b> Non-Compliance; <b>Follow Up:</b> Observations requiring follow-Up actions <b>N/A:</b> Not Applicable					
<b>Section 1: Water Quality</b>						
1.01	Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02	Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03	Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04	Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07	Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08	As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.09	Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.10	Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12	Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13	Are wheel washing facilities well maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.14	Is runoff from wheel washing facilities avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.15	Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Are the vehicle and plant servicing areas paved and located within roofed areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.18	Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19	Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20	Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.21	Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.22	Are the oil interceptors/grease traps maintained properly?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.23	Is used bentonite recycled where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>Section 2: Air Quality</b>							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must be removed from the site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 3: Noise</b>							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 4: Waste/Chemical Management</b>							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.06	Are the chemical waste containers and storage area properly labelled?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.08	Is the chemical container or equipment provided with drip tray?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will be managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	


Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable		Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Section 5: Landscape &amp; Visual</b>							
5.01	Are retained and transplanted trees in health condition?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
5.02	Are retained and transplanted trees properly protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03	Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is damage to trees outside site boundary due to construction activities avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 6: Others</b>							
6.01	Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

(Sok Kwu Wan)


Remarks:

Findings of Site Inspection: (18 February 2014)

Follow up (18 February 2014)

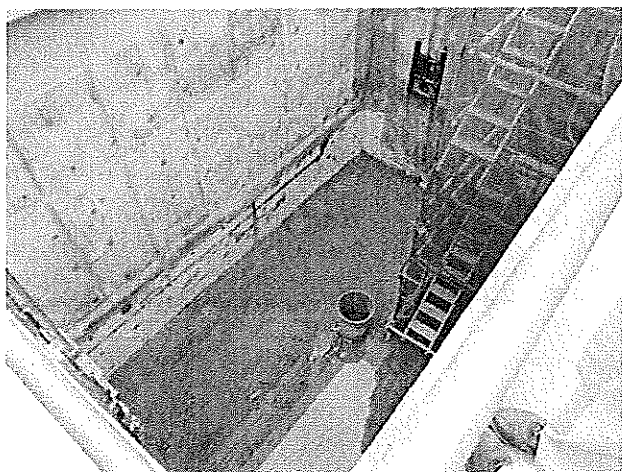

Stagnant water was observed, the Contractor was reminded to spray larvicidal oil for mosquito breeding prevention.

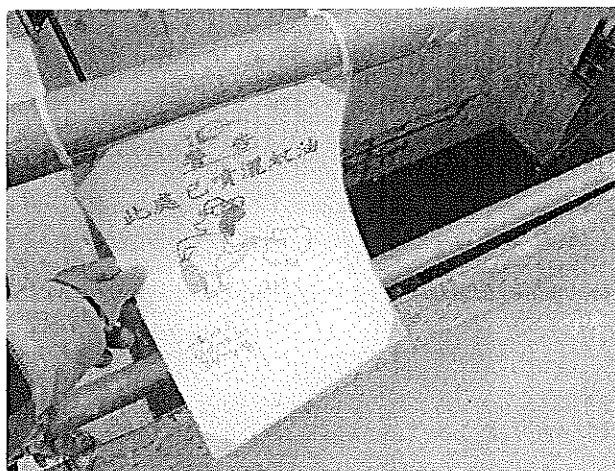

Larvicidal oil was sprayed to stagnant water.

IEC's representative RE's representative ET's representative EO's representative Contractor's representative

( ) (Mr. Daniel Chau) ( Mr. Martin Li ) ( Mr. M.K. Leung ) ( )

Project: TCS/00512/09  
DC-2009-13: Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan

Inspected by  
 ETL/ ET's Representative  
 RE's Representative  
 Contractor's Representative  
 IEC's Representative

Checklist No. TCS512B-25 Feb 2014  
 Mr. Martin Li  
 Mr. Daniel Chau  
 Mr. M.K. Leung

Date: 25 February 2014

Time: 11:00

**PART A:**

**GENERAL INFORMATION**

**Environmental Permit No.**

Weather:  Sunny  Fine  Cloudy  Rainy  
 Temperature: 18.7 °C  
 Humidity:  High  Moderate  Low  
 Wind:  Strong  Breeze  Light  Calm

EP- 281/2007A

**Area Inspected**

1 Sok Kwu Wan

**PART B:**

**SITE AUDIT**

<b>Note:</b> Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable		Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Section 1: Water Quality</b>							
1.01	Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02	Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03	Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04	Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07	Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08	As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.09	Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.10	Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12	Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13	Are wheel washing facilities well maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.14	Is runoff from wheel washing facilities avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.15	Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Are the vehicle and plant servicing areas paved and located within roofed areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.18	Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19	Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20	Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.21	Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.22	Are the oil interceptors/grease traps maintained properly?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.23	Is used bentonite recycled where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>Section 2: Air Quality</b>							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must be removed from the site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 3: Noise</b>							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 4: Waste/Chemical Management</b>							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.06	Are the chemical waste containers and storage area properly labelled?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.08	Is the chemical container or equipment provided with drip tray?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will be managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	



Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable		Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
<b>Section 5: Landscape &amp; Visual</b>							
5.01	Are retained and transplanted trees in health condition?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
5.02	Are retained and transplanted trees properly protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03	Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is damage to trees outside site boundary due to construction activities avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
<b>Section 6: Others</b>							
6.01	Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

(Sok Kwu Wan)

Remarks:

Findings of Site Inspection: (25 February 2014)

Follow up ( 25 February 2014 )

No environmental issue was observed during the site inspection

Nil.

IEC's representative      RE's representative      ET's representative      EO's representative      Contractor's representative

( )      (Mr. Daniel Chau)      ( Mr. Martin Li )      ( Mr. M.K. Leung)      ( )

## **Appendix M**

### **Implementation Schedule of Mitigation Measures**

### Implementation Schedule of Air Quality Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages**			Relevant Legislation & Guidelines
					D	C	O	
<b>Construction Phase</b>								
3.32	2.34	Installation of 2m high solid fences around the construction site of Pumping Station P2.	Work site / during construction	Contractor		√		
3.34	2.34	Adopting the following good site practices and follow the dust control requirements of the Air Pollution Control (Construction Dust) Regulation: <ul style="list-style-type: none"> <li>• Stockpiles of imported material kept on site should be contained within hoardings, dampened and / or covered during dry and windy weather;</li> <li>• Material stockpiled alongside trenches should be covered with tarpaulins whenever works are close to village houses;</li> <li>• Water sprays should be used during the delivery and handling of cement, sands, aggregates and the like.</li> <li>• Any vehicle used for moving sands, aggregates and construction waste should have properly fitting side and tail boards. Materials should not be loaded to a level higher than the side and tail boards, and should be covered by a clean tarpaulin.</li> </ul>	Work site / during construction	All contractors		√		EIAO-TM, APCO, Air Pollution Control (Construction Dust) Regulation
3.36	Section 2	1 hour and 24 hour dust monitoring and site audit	Designated air monitoring locations / throughout construction period	Contractor/ Environmental Team		√		EM&A Manual

\* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

\*\* D=Design, C=Construction, O=Operation

N/A Not applicable

### Implementation Schedule of Noise Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location/Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
<b>Construction Phase</b>								
4.41-4.43	3.19	<ul style="list-style-type: none"> <li>• Use of quiet PME for the construction of the pumping stations</li> <li>• Use of temporary noise barrier during the construction of Pumping Station P1a</li> </ul>	Work site /during the construction of Pumping Stations	Contractor		√		EIAO-TM, NCO
4.44 – 4.49	3.19	Implementation of following measures during the sewer construction: <ul style="list-style-type: none"> <li>• Use of quiet PME or method;</li> <li>• Restriction on the number plant (1 item for each type of plant); and</li> <li>• Good Site Practices                             <ul style="list-style-type: none"> <li>➤ Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program.</li> <li>➤ Mobile plant, if any, should be sited as far away from NSRs as possible.</li> <li>➤ Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.</li> <li>➤ Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.</li> <li>➤ Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities.</li> </ul> </li> </ul>	Work site /during the construction of Sewer.	Contractor		√		

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location/Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
4.50 – 4.53	3.19	<ul style="list-style-type: none"> <li>Use of noise screening structures such as acoustic shed and barrier wherever practicable and feasible in areas with sufficient clearance and headroom.</li> <li>Adoption of manual working method wherever practicable and feasible in areas where the worksites of the proposed sewer alignment are located less than 20 m from the residential NSRs and less than 30 m from the temple (THT) and the public library.</li> <li>Use of PME for the construction of the section of sewer between the NSR and the Pumping Station P1a should not be allowed during the excavation work of Pumping Station P1a.</li> </ul>	Work site /during the construction of Sewer.	Contractor		√		
4.60	Section 35	Noise monitoring	Designated noise monitoring locations / throughout construction period	Contractor/ Environmental Team		√		EM&A Manual

\* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.  
 \*\* D=Design, C=Construction, O=Operation  
 N/A Not applicable

### Implementation Schedule of Water Quality Control Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location (duration /completion of measures)	Implementation Agent	Implementation Stages**			Relevant Legislation and Guidelines
					D	C	O	
<b>Construction Phase</b>								
5.77	4.35	No-dig method using Horizontal Directional Drilling (HDD) would be used for the installation of outfall pipe of about 480 m from shore to minimize the potential water quality impacts arising from the dredging works required for the submarine outfall construction.  Silt curtains will be installed around the exit area of the pilot drill.	Marine works site / During construction of submarine outfall	Contractor		√		
5.73 – 5.78	4.36	Dredging Works  Implementation of following measures during the dredging works: <ul style="list-style-type: none"> <li>• dredging should be undertaken using closed grab dredgers with a maximum total production rate of 55m<sup>3</sup>/hr;</li> <li>• deployment of 2-layer silt curtains with the first layer enclosing the grab and the second layer at around 50m from the dredging area while dredging works are in progress;</li> <li>• dredging operation should be undertaken during ebb tide only;</li> <li>• all vessels should be sized such that adequate clearance (i.e. minimum clearance of 0.6m) is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash;</li> <li>• all pipe leakages should be repaired promptly and plant should not be operated with leaking pipes;</li> <li>• excess material should be cleaned from the decks and exposed fittings of barges before the vessel is moved;</li> <li>• adequate freeboard (i.e. minimum of 200mm) should be maintained on barges to ensure that decks are not washed by wave action;</li> <li>• all barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material;</li> <li>• loading of barges should be controlled to prevent splashing of dredged material to the surrounding water, and barges should not be filled to a level which will cause the overflow of materials or polluted water during loading or transportation; and</li> </ul>	Marine works site and at the identified water sensitive receivers/ During construction	Contractor		√		

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location (duration /completion of measures)	Implementation Agent	Implementation Stages**			Relevant Legislation and Guidelines
					D	C	O	
		<ul style="list-style-type: none"> <li>the decks of all vessels should be kept tidy and free of oil or other substances that might be accidentally or otherwise washed overboard.</li> </ul>						
5.79	4.37	<p><u>Construction Run-off and Drainage</u></p> <p>Implementation of the following site practices outlined in ProPECC PN 1/94 for “Construction Site Drainage”</p> <ul style="list-style-type: none"> <li>Provision of perimeter channels to intercept storm-runoff from outside the site. These should be constructed in advance of site formation works and earthworks.</li> <li>Works programmes should be designed to minimize works areas at any one time, thus minimizing exposed soil areas and reducing the potential for increased siltation and runoff.</li> <li>Sand / silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove the sand / silt particles from run-off. These facilities should be properly and regularly maintained. These facilities should be carefully planned to ensure that they would be installed at appropriate locations to capture all surface water generated on site.</li> <li>Careful programming of the works to minimise soil excavation works during rainy seasons.</li> <li>Exposed soil surface should be protected by paving or hydroseeding as soon as possible to reduce the potential of soil erosion.</li> <li>Trench excavation should be avoided in the wet season, and if necessary, these should be excavated and backfilled in short sections.</li> <li>Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric</li> </ul>	Construction works sites	Contractor		√		ProPECC PN 1/94
5.80	4.38	<p><u>General Construction Activities</u></p> <p>Debris and rubbish generated on-site should be collected, handled and disposed of properly to avoid entering the nearby coastal waters and stormwater drains. All fuel tanks and storage areas should be provided</p>	Construction works sites	Contractor		√		

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location (duration /completion of measures)	Implementation Agent	Implementation Stages**			Relevant Legislation and Guidelines
					D	C	O	
		with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. Open drainage channels and culverts near the works areas should be covered to block the entrance of large debris and refuse.						
5.81	4.39	<u>Wastewater Arising from Workforce</u> Portable toilets should be provided by the Contractors, where necessary, to handle sewage from the workforce. The Contractor should also be responsible for waste disposal and maintenance practices.	Construction works sites	Contractor		√		
5.96	Section 4	Water quality monitoring	Designated water monitoring locations/ throughout construction period	Contractor		√		EM&A Manual

\* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

\*\* D=Design, C=Construction, O=Operation

N/A Not applicable



### Implementation Schedule of Sediment Contamination Mitigation Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages**			Relevant Legislation & Guidelines
					D	C	O	
6.17	5.3	Follow the requirement and procedures for dredged mud disposal specified under the WBTC No. 34/2002.	Marine works site / during dredging works	Contractor		√		WBTC No. 34/2002
6.18	5.4	Implement appropriate dredging methods which have been incorporated into the recommended water quality mitigation measures.	Marine works site, during dredging works	Contractor		√		
6.19	5.5	During the transportation and disposal of the dredged sediment, the following measures should be taken: <ul style="list-style-type: none"> <li>Bottom opening of barges should be fitted with tight fitting seals to prevent leakage of material. Excess material should be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.</li> <li>Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels should be equipped with automatic self monitoring devices as specified by the DEP.</li> </ul>	Marine works site and at the identified sensitive receivers	Contractor		√		

\* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

\*\* D=Design, C=Construction, O=Operation

N/A Not applicable

### Implementation Schedule of Solid Waste Management Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
<b>Construction Phase</b>								
7.14	6.4	<u>Good site practices</u> <ul style="list-style-type: none"> <li>Nomination of an approved person, such as a site manager, to be responsible for implementation of good site practices, arranging for collection and effective disposal to an appropriate facility, of all wastes generated at the site</li> <li>Training (proper waste management and chemical handling procedure) should be provided for site staffs</li> <li>Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.</li> <li>Provision of sufficient waste disposal points and regular collection for disposal.</li> <li>Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility.</li> <li>Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.</li> <li>Maintain records of the quantities of wastes generated, recycled and disposed.</li> </ul>	Work sites/During construction	Contractor		√		Waste Disposal Ordinance (Cap.54)
7.15	6.5	To monitor the disposal of C&D waste at landfills and to control fly tipping, a trip-ticket system should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. An Independent Environmental Checker should be responsible for auditing the results of the system.	Work sites/During construction	Contractor		√		WBTC No. 21/2002
7.16	6.6	Recommendations to achieve waste reduction include: <ul style="list-style-type: none"> <li>segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>to encourage collection of aluminium cans by individual collectors, separate labelled bins should be provided to segregate this waste from other general refuse generated</li> </ul>	Work sites/During construction	Contractor		√		WBTC No. 4/98, 5/98

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
		by the work force; <ul style="list-style-type: none"> <li>any unused chemicals or those with remaining functional capacity should be recycled;</li> <li>use of reusable non-timber formwork to reduce the amount of C&amp;D material;</li> <li>prior to disposal of C&amp;D waste, it is recommended that wood, steel and other metals should be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill;</li> <li>proper storage and site practices to minimise the potential for damage or contamination of construction materials; and</li> <li>plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.</li> </ul>						
7.18	6.7	<u>General Site Wastes</u> <ul style="list-style-type: none"> <li>A collection area for construction site waste should be provided where waste can be stored prior to removal from site</li> <li>An enclosed and covered area for the collection of the waste is recommended to reduce 'wind blow' of light material</li> </ul>	Work sites/During construction	Contractor		√		Public Health and Municipal Services Ordinance (Cap. 132)
7.19-7.20	6.8 – 6.9	<u>Chemical Wastes</u> <ul style="list-style-type: none"> <li>After use, chemical waste should be handled according to the Code of Practice on the Package, Labelling and Storage of Chemical Wastes</li> <li>Any unused chemicals or those with remaining functional capacity should be recycled</li> <li>Waste should be properly stored on site within suitably designed containers and should be collected by an approved licensed waste collectors for disposal at the Chemical Waste Treatment Facility or other licenced facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation under the Waste Disposal Ordance.</li> </ul>	Work sites/During construction	Contractor		√		Waste Disposal (Chemical Waste) (General) Regulation, Code of Practice on the Packaging Labelling and Storage of Chemical Wastes

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
		<ul style="list-style-type: none"> <li>Any service shop and minor maintenance facilities should be located on hard standing within a bunded area, and sumps and oil interceptors should be provided.</li> <li>Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should be undertaken within the designated areas equipped control these discharges</li> </ul>						
7.21-7.22	6.10 – 6.11	<p><u>Construction and Demolition Material</u></p> <ul style="list-style-type: none"> <li>The C&amp;D waste should be separated on-site into three categories: <ul style="list-style-type: none"> <li>➤ public fill, the inert portion of the C&amp;D material (e.g. concrete and rubble), which should be re-used on-site or disposed of at a public filling area;</li> <li>➤ C&amp;D waste for re-use and / or recycling, the non-inert portion of the C&amp;D material, (e.g. steel and other metals, woods, glass and plastic);</li> <li>➤ C&amp;D waste which cannot be re-used and / or recycled (e.g. wood, glass and plastic)</li> </ul> </li> <li>Where possible, inert material should be re-used on-site</li> <li>Where practicable, steel and other metals should be separated for re-use and/or recycling prior to disposal of C&amp;D material</li> </ul>	During all construction phases	Contractors		√		WBTC No. 4/98, 5/98, 21/2002, 25/99, 12/2000

\* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

\*\* D=Design, C=Construction, O=Operation

N/A Not applicable

### Implementation Schedule of Ecological Impact Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages			Relevant Legislation & Guidelines
					D	C	O	
<b>Construction Phase</b>								
8.157	7.2	<u>Terrestrial Ecology</u> <ul style="list-style-type: none"> <li>Labeling and fencing of the uncommon tree species</li> <li>Avoidance of use of woodland habitats as Works Area, in particular where trees are located</li> </ul>	Work sites / during construction phase	Contractor		√		
8.159 – 8.160	7.3	<u>Subtidal Ecology</u> Use of HDD technique  Dredging <ul style="list-style-type: none"> <li>Use of closed-grab dredger</li> <li>Deploy silt curtains during dredging.</li> </ul>	Marine works site / during dredging works	Contractor		√		
8.161	7.4	Site runoff <ul style="list-style-type: none"> <li>Construction and maintenance of sand / silt removal facilities</li> <li>Silt curtains</li> <li>Timing of earthworks</li> <li>Coverage of sand / fill piles during storms.</li> <li>Barriers along the landward side of Pumping Station P2 site boundary (to prevent site runoff from entering area with Romer's Tree Frog)</li> </ul>	All work sites / during construction phase	Contractor		√		

\* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

\*\* D=Design, C=Construction, O=Operation

N/A Not applicable

### Implementation Schedule of Fisheries Impact Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages**			Relevant Legislation & Guidelines
					D	C	O	
9.29	8.3	Use of closed grab dredging and silt curtains around the immediate dredging area and low dredging rates as recommended in Water Quality of the EIA report	Marine works site, during dredging works	Contractor		√		TM on EIA Process
9.32	Section 8	Water quality monitoring (see Implementation Schedule for Water Quality Control Measures)	Designated monitoring locations / throughout construction period and 1 year following operation of the STW	Contractor and Environmental Team		√	√	EM&A Manual

\* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

\*\* D=Design, C=Construction, O=Operation

N/A Not applicable

### Implementation Schedule of Landscape and Visual Impact Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
<b>Construction Phase</b>								
10.74	9.10	Retaining existing trees and minimizing damage to vegetation by close coordination and on site alignment adjusted of rising main and gravity sewer pipelines.	All sites	Contractor		√		WBTC No. 14/2002
		Careful and efficient transplanting of affected trees to temporary or final transplant location (the proposed tree to be transplanted is a semi-mature <i>Macaranga tanarius</i> and is located at the proposed Pumping Station P2 location).	All sites	Contractor		√		WBTC No. 14/2002
		Short excavation and immediate backfilling sections upon completion of works to reduce active site area.	All sites	Contractor		√		
		Screening of site construction works by use of hoarding that is appropriate to its site.	All sites	Contractor		√		WBTC No. 19/2001
		Conservation of topsoil for reuse.	All sites	Contractor		√		
		Night-time light source from marine fleets should be directed away from the residential units.	Outfall area.	Contractor		√		

\* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

\*\* D=Design, C=Construction, O=Operation

N/A Not applicable

**Appendix N**

**Tree Inspection Report**



經緯園藝有限公司

Melofield Nursery & Landscape Contractor Ltd

元朗下攸田村 125 號 125, Ha Yau Tin Tsuen, Yuen Long, N.T.

TEL: (852) 2572-0048 FAX: (822)2573-9099 E-mail: melofield@netvigator.com

Contract No. DC/2009/13

Project Name: Construction of Sewage Treatment  
Works at Yung Shue Wan and Sok Kwu Wan

## Sok Kwu Wan




**Tree Inspection Report for *Celtis timorensis***

**Inspection Date : 30-01-2014**



## 1. Introduction

According to the requirement in the Environmental Permit EP-281/2007/A, the uncommon tree species, *Celtis timorensis*, found in the pumping station P1b area as shown in figure below shall be properly transplanted to the area immediately south of the Pumping Station P1b before commencement of construction of the Pumping Station P1b

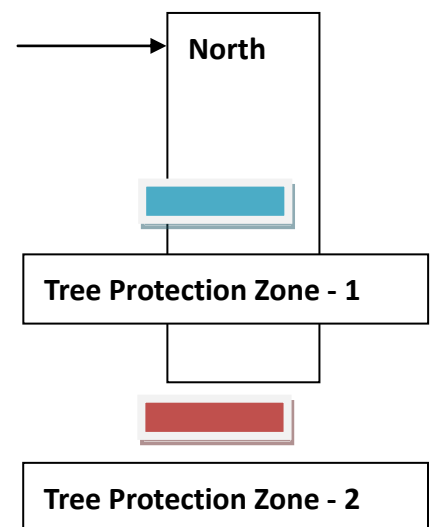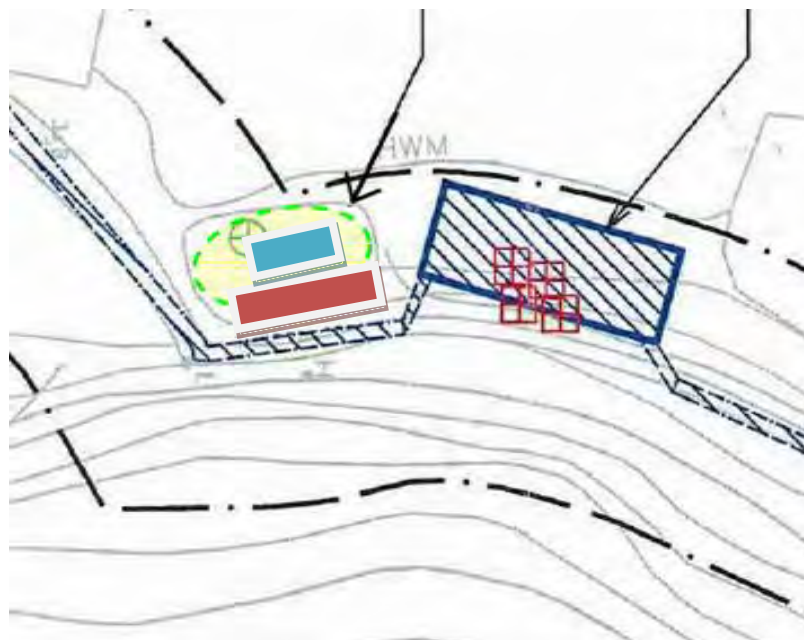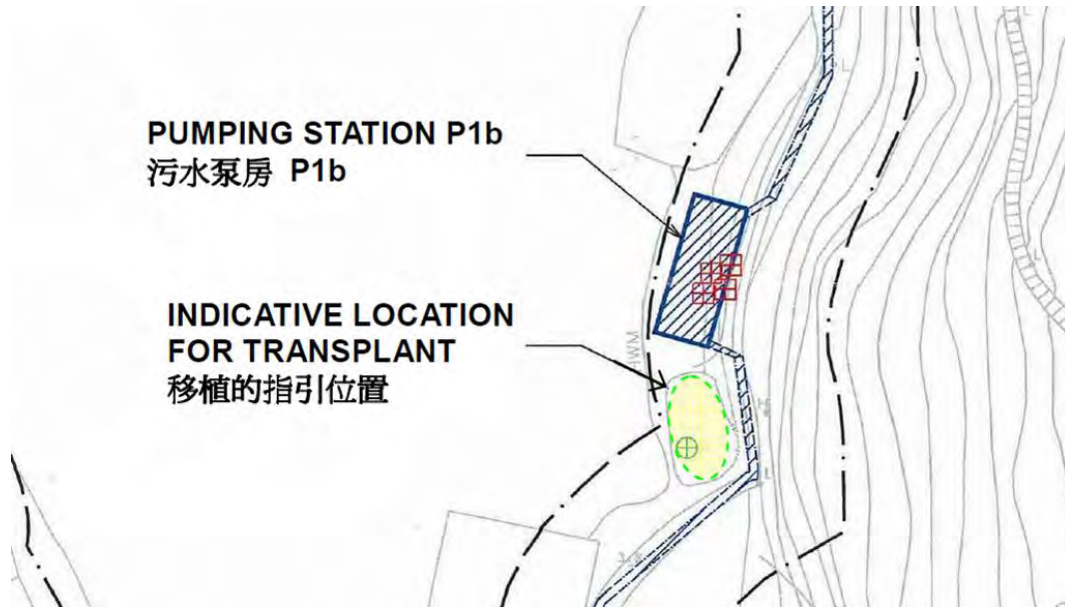

This Tree Inspection Report describes the bi weekly monitoring result of the *Celtis timorensis*, which were additionally planted as the compensation of previously transplanted *Celtis timorensis* CT7, CT8, CT9 & CT10.

## 2. Summary of Inspection

Date of Inspection	30 January 2014, around 15:30
Location	A soil ground adjacent to the Pumping Station P1b Chung Mei, at Sok Kwu Wan, Lamma Island.
Weather	Sunny, the vegetations are located under the shade of existing tall trees.
The labeled <i>Celtis timorensis</i> under Tree Protection Zone 2	CT_5A & CT_6A

## 3. Proposed Inspection Schedule

Month	Actual / proposed Inspection Date
October, 2011	10 and 24 October 2011
November, 2011	8 November 2011
December, 2011	14 and 30 December 2011
January 2012	31 January 2012
February 2012	15 and 29 February 2012
March 2012	15 and 31 March 2012
April 2012	16 and 30 April 2012
May 2012	15 and 31 May 2012
June 2012	15 and 30 June 2012
July 2012	16 and 30 July 2012
August 2012	15 and 31 August 2012
September 2012	15 and 29 September 2012
October 2012	15 and 31 October 2012
November 2012	15 and 30 November 2012
December 2012	15 and 30 December 2012
January 2013	15 and 30 January 2013
February 2013	15 and 28 February 2013
March 2013	15 and 30 March 2013
April 2013	15 and 30 April 2013
May 2013	15 and 30 May 2013
June 2013	15 and 29 June 2013

July 2013	15 and 31 July 2013
August 2013	15 and 31 August 2013
September 2013	14 and 30 September 2013
October 2013	15 and 31 October 2013
November 2013	15 and 30 November 2013
December 2013	14 and 31 December 2013
January 2014	15 and 30 January 2014

#### 4. Summary of Inspection Result

Tree No	Speciation	Health Status
CT_5A	<i>Celtis timorensis</i>	Good
CT_6A	<i>Celtis timorensis</i>	Good


#### Inspection parameters or criteria

**Good** Leaves and stem grown very lush, additional or larger in size of leaves can be observed in each inspection

**Fair** Green leaves can be found. No major unhealthy condition of the plant is observed. The condition is stable.

**Poor** Fewer green leaves than usual are observed. No new leaf is grown and the condition keep stable. The bark is dry. The plant is weak.


**Very Poor** No new green leaf or bud can be observed. The bark is dry. The plant is weak.

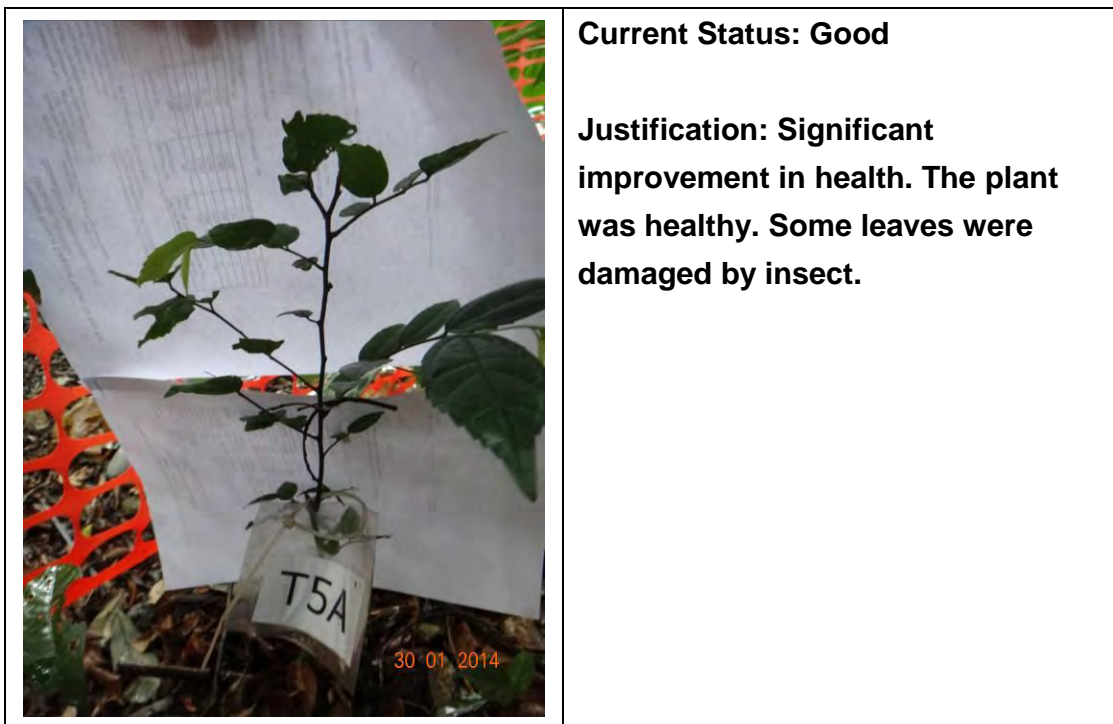

**5. Description of Inspection Results:**

**Tree ID: CT\_5A**

**Tree ID: CT\_6A**

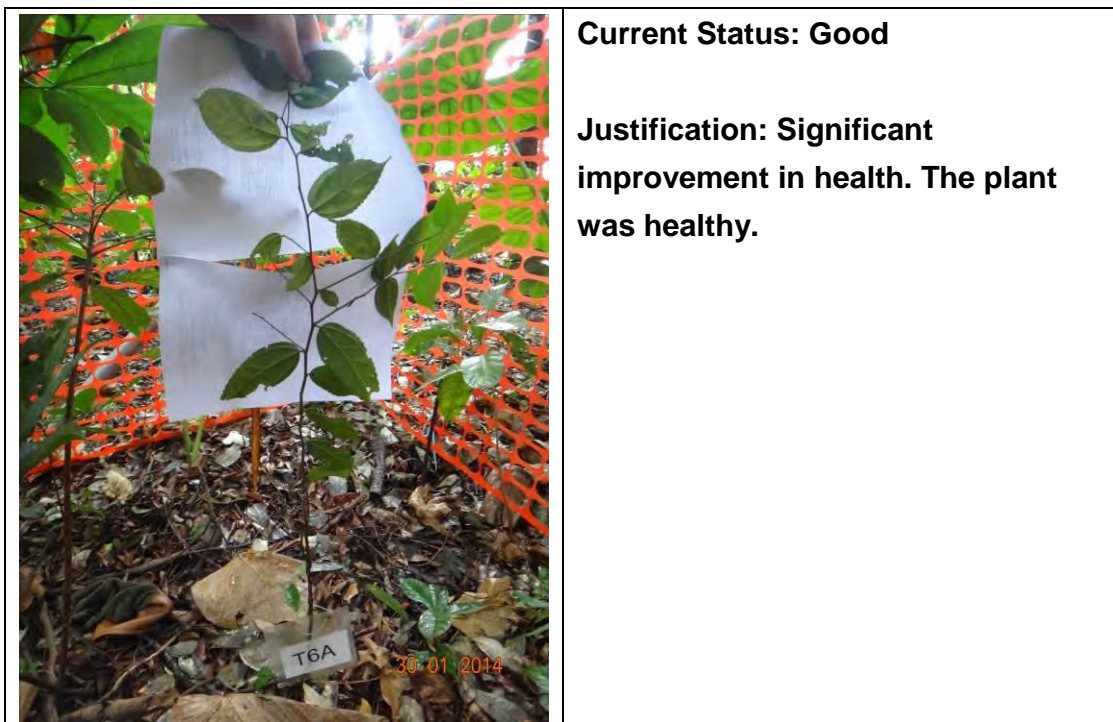

### **Overall Condition**

In the Tree Protection Zone 2, The health of CT\_5A and CT\_6A were found satisfactory. Regular watering and weeding will be carried out during dry weather. They may better recover under this warm and rainy weather. Some newly grown green leaves were found eaten by insects. Remove any insect found on the plant physically to prevent the bud attacked by leaf-feeding insect. No pesticide should be used when the plants are weak.

Considering CT2A, CT3A were lost due to typhoon, compensatory of additional *Celtis timorensis* is proposed and will be carried out in the coming warm weather season for better growing.

經緯園藝有限公司

Melofield Nursery & Landscape Contractor Ltd

元朗下攸田村 125 號 125, Ha Yau Tin Tsuen, Yuen Long, N.T.

TEL: (852) 2572-0048 FAX: (822)2573-9099 E-mail: melofield@netvigator.com

Contract No. DC/2009/13

Project Name: Construction of Sewage Treatment  
Works at Yung Shue Wan and Sok Kwu Wan

## Sok Kwu Wan


**Tree Inspection Report for *Celtis timorensis***

**Inspection Date : 15-02-2014**



## 1. Introduction

According to the requirement in the Environmental Permit EP-281/2007/A, the uncommon tree species, *Celtis timorensis*, found in the pumping station P1b area as shown in figure below shall be properly transplanted to the area immediately south of the Pumping Station P1b before commencement of construction of the Pumping Station P1b

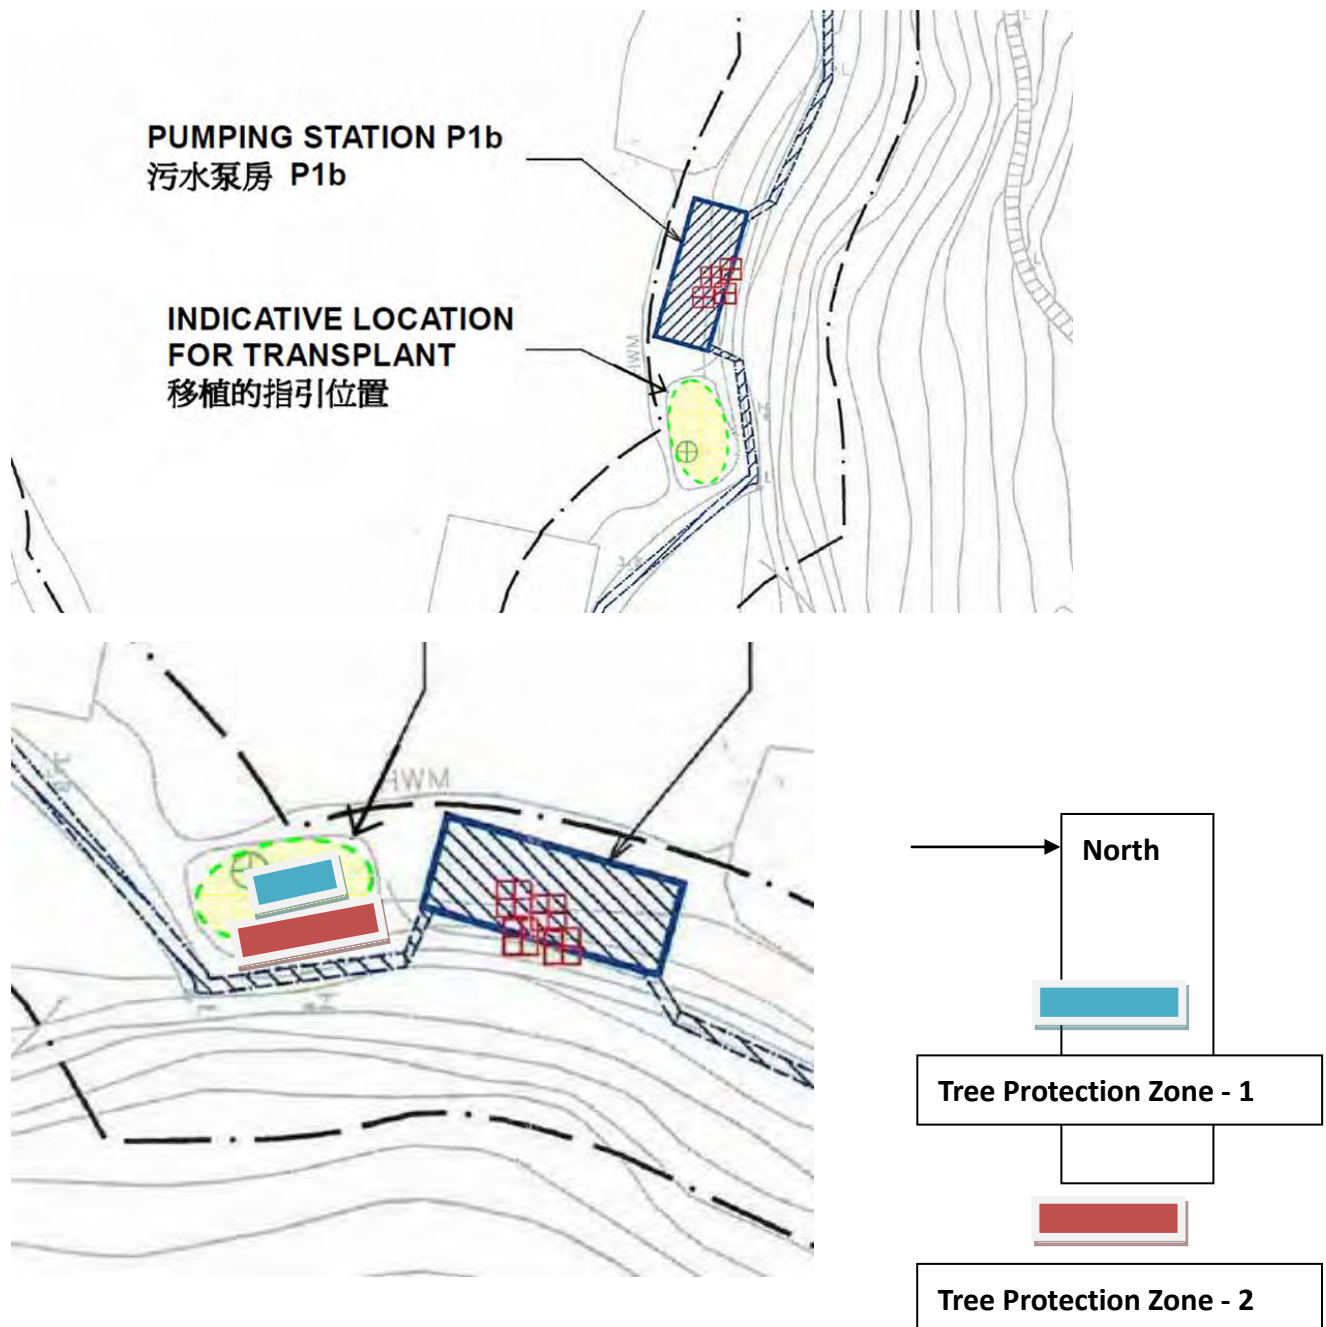



This Tree Inspection Report describes the bi weekly monitoring result of the *Celtis timorensis*, which were additionally planted as the compensation of previously transplanted *Celtis timorensis* CT7, CT8, CT9 & CT10.

## 2. Summary of Inspection

Date of Inspection	15 February 2014, around 15:30
Location	A soil ground adjacent to the Pumping Station P1b Chung Mei, at Sok Kwu Wan, Lamma Island.
Weather	Cloudy, the vegetations are located under the shade of existing tall trees.
The labeled <i>Celtis timorensis</i> under Tree Protection Zone 2	CT_5A & CT_6A

## 3. Proposed Inspection Schedule

Month	Actual / proposed Inspection Date
October, 2011	10 and 24 October 2011
November, 2011	8 November 2011
December, 2011	14 and 30 December 2011
January 2012	31 January 2012
February 2012	15 and 29 February 2012
March 2012	15 and 31 March 2012
April 2012	16 and 30 April 2012
May 2012	15 and 31 May 2012
June 2012	15 and 30 June 2012
July 2012	16 and 30 July 2012
August 2012	15 and 31 August 2012
September 2012	15 and 29 September 2012
October 2012	15 and 31 October 2012
November 2012	15 and 30 November 2012
December 2012	15 and 30 December 2012
January 2013	15 and 30 January 2013
February 2013	15 and 28 February 2013
March 2013	15 and 30 March 2013
April 2013	15 and 30 April 2013
May 2013	15 and 30 May 2013
June 2013	15 and 29 June 2013

July 2013	15 and 31 July 2013
August 2013	15 and 31 August 2013
September 2013	14 and 30 September 2013
October 2013	15 and 31 October 2013
November 2013	15 and 30 November 2013
December 2013	14 and 31 December 2013
January 2014	15 and 30 January 2014
February 2014	15 February 2014

#### 4. Summary of Inspection Result

Tree No	Speciation	Health Status
CT_5A	<i>Celtis timorensis</i>	Good
CT_6A	<i>Celtis timorensis</i>	Good

#### Inspection parameters or criteria

- Good** Leaves and stem grown very lush, additional or larger in size of leaves can be observed in each inspection
- Fair** Green leaves can be found. No major unhealthy condition of the plant is observed. The condition is stable.
- Poor** Fewer green leaves than usual are observed. No new leaf is grown and the condition keep stable. The bark is dry. The plant is weak.
- Very Poor** No new green leaf or bud can be observed. The bark is dry. The plant is weak.



**Current Status: Good**

**Justification: Significant improvement in health. The plant was healthy. Some leaves were damaged by insect.**

### 5. Description of Inspection Results:

**Tree ID: CT\_5A**

**Tree ID: CT\_6A**



**Current Status: Good**

**Justification: Significant improvement in health. The plant was healthy.**

### **Overall Condition**

In the Tree Protection Zone 2, The health of CT\_5A and CT\_6A were found satisfactory. Regular watering and weeding will be carried out during dry weather. They may better recover under this warm and rainy weather. Some newly grown green leaves were found eaten by insects. Remove any insect found on the plant physically to prevent the bud attacked by leaf-feeding insect. No pesticide should be used when the plants are weak.

Considering CT2A, CT3A were lost due to typhoon, compensatory of additional *Celtis timorensis* is proposed and will be carried out in the coming warm weather season for better growing.
