

Construction of a Secondary Boundary Fence and  
New Sections of Primary Boundary Fence and  
Boundary Patrol Road

Improvement Works for Mai Po, Lok Ma Chau, Sha  
Tau Kok and Planting Works at Tak Yuet Lau –  
Monthly EM&A Report for September 2015

October 2015  
Architectural Services Department





# Construction of a Secondary Boundary Fence and New Sections of Primary Boundary Fence and Boundary Patrol Road

Improvement Works for Mai Po, Lok Ma Chau, Sha Tau Kok and  
Planting Works at Tak Yuet Lau – Monthly EM&A Report for  
September 2015

October 2015

Architectural Services Department

39/F Queensway Government Offices, 66 Queensway, Hong Kong



**Pursuant to Condition 4.5 of Environmental Permit No. EP-347/2009/A,  
this Monthly EM&A Report for September 2015 has been certified by the  
Environmental Team Leader and verified by the Independent  
Environmental Checker as having complied with the requirements as set  
out in the EM&A Manual.**

**Certified by:**



\_\_\_\_\_  
Brandon Wong  
Environmental Team Leader (ETL)  
Mott MacDonald Hong Kong Limited

**Date**

22 October 2015

**Verified by:**



\_\_\_\_\_  
David Yeung  
Independent Environmental Checker (IEC)  
Ramboll Environ Hong Kong Limited

**Date**

9 November 2015



# Content

<b>Chapter</b>	<b>Title</b>	<b>Page</b>
	Executive Summary	i
<b>1.</b>	<b>Introduction</b>	<b>1</b>
1.1	Background	1
1.2	Project Organisation	3
1.3	Works Undertaken in the Reporting Month	3
<b>2.</b>	<b>EM&amp;A Requirements</b>	<b>4</b>
2.1	Summary of EM&A Requirements	4
2.2	Implementation of Environmental Mitigation Measures	4
<b>3.</b>	<b>Noise Impact Monitoring</b>	<b>5</b>
3.1	Monitoring Parameters, Frequency and Duration	5
3.2	Monitoring Location	5
3.3	Monitoring Equipment	6
3.4	Equipment Calibration	6
3.5	Monitoring Methodology	6
3.5.1	Field Monitoring	6
3.5.2	Maintenance and Calibration	7
3.6	Results of Impact Monitoring	7
<b>4.</b>	<b>Environmental Site Inspection and Audit</b>	<b>8</b>
4.1	Site Inspections	8
4.2	Environmental Meetings	8
4.3	Status of Environmental Submissions, Permits and Licences	8
4.4	Advice on the Solid and Liquid Waste Management Status	9
4.5	Review of Environmental Monitoring Procedures	9
4.6	Implementation Status of Environmental Mitigation Measures	9
<b>5.</b>	<b>Record of Non-compliance, Complaints, Notifications of Summons and Successful Prosecutions</b>	<b>10</b>
5.1	Non-compliance of Action and Limit Levels	10
5.2	Environmental Complaints	10
5.3	Notifications of Summons and Successful Prosecutions	10
<b>6.</b>	<b>Future Key Issues</b>	<b>11</b>
6.1	Construction Programme for the Next Reporting Month	11
6.2	Key Issues for the Next Reporting Month	11
6.3	Monitoring Schedule for the Next Reporting Month	12
<b>7.</b>	<b>Conclusions and Recommendations</b>	<b>13</b>
7.1	Conclusions	13

7.2	Recommendations	13
-----	-----------------	----

## Appendices 14

Appendix A.	Construction Works Programme	15
Appendix B.	Project Organisation Chart	16
Appendix C.	Environmental Quality Performance Limits	17
Appendix D.	Event and Action Plans	18
Appendix E.	Schedule of Mitigation Measures from the EIA Report and EM&A Manual	19
Appendix F.	EM&A Schedule	30
Appendix G.	Calibration Certificates	32
Appendix H.	Noise Monitoring Results and Graphical Presentation	33
Appendix I.	Monthly Waste Flow Table	34
Appendix J.	Complaint Log	37
Appendix K.	Weather Information from Hong Kong Observatory	38

## Figures

- Figure 1.1: General Layout Plan  
 Figure 2.1: Location of Noise Monitoring Stations

## Tables

Table 2.1:	Summary of EM&A Impact Requirements	4
Table 3.1:	Noise Monitoring Parameters, Frequency and Duration	5
Table 3.2:	Noise Impact Monitoring Location	6
Table 3.3:	Noise Monitoring Equipment	6
Table 3.4:	Noise Monitoring Equipment Calibration Frequencies	6
Table 4.1:	Summary of Environmental Site Inspections	8
Table 4.2:	Status of Environmental Permits and Licences	8
Table 4.4:	Implementation Schedule of Mitigation Measures	9
Table C.1:	Action and Limit Levels for Construction Noise	17
Table D.1:	Event and Action Plan for Construction Noise	18
Table E.1:	Recommended Mitigation Measures – Air Quality	19
Table E.2:	Recommended Mitigation Measures – Noise	20
Table E.3:	Recommended Mitigation Measures – Water Quality	21
Table E.4:	Recommended Mitigation Measures – Waste Management	23
Table E.5:	Recommended Mitigation Measures – Ecology	25
Table E.6:	Recommended Mitigation Measures – Landscape and Visual	26
Table I.1:	Monthly Summary Waste Flow Table for 2015 (from April)	34
Table J.1:	Complaint Log for the Reporting Month	37



# Executive Summary

Mott MacDonald Hong Kong Limited (MMHK) has been commissioned by the Architectural Services Department (ArchSD) as the Environmental Team (ET) to carry out Environmental Monitoring and Audit (EM&A) services for improvement works along the boundary in the Frontier Closed Area (FCA) and planting works at Tak Yuet Lau (the subject works), which form part of the “Construction of a Secondary Boundary Fence and New Sections of Primary Boundary Fence and Boundary Patrol Road” (the Project).

This Monthly EM&A Report covers the works carried out during the reporting month from 1 to 30 September 2015 and presents a summary of the environmental monitoring and audit works, list of activities, and mitigation measures implemented during the same period.

## Site Activities

The following major construction activities took place during the reporting month:

### ***Improvement Works for Boundary Fence at Mai Po, Lok Ma Chau and Sha Tau Kok:***

- Removal of topsoil at Mai Po Section

### ***Landscaping Works at Tak Yuet Lau:***

- Tree planting
- Shrub planting
- Hydroseeding

## Breach of Action and Level Limits

There was no breach of Action or Limit levels for noise level (measured as  $L_{eq}$ ) in the reporting month.

## Complaints

There was no record of complaints received in the reporting month.

## Notification of Summons and Successful Prosecutions

There was no record of Notification of summons and successful prosecution in the reporting month.

## Reporting Changes

There are no reporting changes in the reporting month.

## Future Key Issues

Future key issues to be considered in the forthcoming month include:

### ***Air***

- Regular maintenance of all plant and equipment;

- Handling of any excavated dusty materials or stockpile of dusty material; and
- Spraying of water prior to any loading, unloading or transfer of dusty materials.

#### **Noise**

- Location of noisy equipment and noisy activities relative to the Noise Sensitive Receivers (NSRs);
- Avoiding the operation of unused equipment, and minimising the use of Powered Mechanical Equipment (PME) and parallel use of noisy equipment / machinery; and
- Regular maintenance of all plant and equipment.

#### **Water Quality**

- No discharge of silty water into the storm drain and drainage channel within and the vicinity of the site;
- Removal off-site of construction plant causing pollution to water system due to leakage of oil or fuel; and
- Temporary stockpiling of excavated soil in a specially designated area with provision of tarpaulin cover.

#### **Waste**

- Control measures at the stockpiling area to prevent the generation of dust and pollution of stormwater channels, fish ponds or river channels;
- Segregation, storage, transportation and disposal of different types of waste; and
- Keeping of records of quantities of wastes generated, recycled and disposal (with locations).

#### **Ecology**

- Good site practices for controlling the dust and water quality; and
- Clear definition of works limit to avoid impact on adjacent habitats.

#### **Landscape and Visual**

- Retain tree with high amenity or ecology value and contributing most to landscape and amenity of site;
- Precautionary area around trees to be retained equal to half of the tree canopy diameter;
- Prohibition of the storage of materials including fuel, the movement of construction vehicles, and the refuelling and washing of equipment including concrete mixers within the precautionary area;
- Pruning of the branches of existing trees identified for transplantation and retention;
- Rectification and repair of damaged vegetation following the construction phase to its original condition;
- Careful monitoring of all works affecting the trees identified for retention and transplantation; and
- Enforcement of construction site controls including storage of materials, location and appearance of site accommodation and the careful design of site lighting to prevent light spillage.

Environmental mitigation measures will be implemented on site as recommended and weekly site audits will be carried out to ensure that the environmental conditions are acceptable.

# 1. Introduction

## 1.1 Background

The Frontier Closed Area (FCA) is an integral part of the package of measures aimed at maintaining the integrity of the boundary of the Hong Kong Special Administrative Region (HKSAR) with mainland China, and combating illegal immigration and other cross-boundary criminal activities. Following a recent review, the HKSAR Government has concluded that with the erection of a secondary boundary fence (SBF) along the boundary patrol road (BPR) and construction of new sections of the BPR and primary boundary fence (PBF) at certain sections along the boundary, the FCA coverage can be substantially reduced without affecting the objective of maintaining the integrity of the boundary.

The erection of the PBF and SBF (hereafter referred to as ‘The Project’) along the northern and southern curbs of the realigned BPR respectively aims to facilitate the Hong Kong Police Force (HKPF) in combating cross-boundary criminal activities. The reduced FCA will comprise a narrow strip of land covering the realigned BPR and areas to its north, together with the points of crossing the boundary (i.e. the Boundary Control Points and Sha Tau Kok town). Areas south of the SBF will generally be excised from the FCA.

An Environmental Impact Assessment (EIA) for the proposed works was carried out under the Environmental Impact Assessment Ordinance (EIAO, Cap 499). An EIA Report and an Environmental Monitoring and Audit (EM&A) Manual were completed in January 2009 and approved by the Environmental Protection Department (EPD) in April 2009 (Register No. AEIAR-136/2009). The entire length of the proposed works is about 21.7 km from west of Pak Hok Chau to east of Sha Tau Kok and is divided into four sections. A general layout plan of the Project site is presented in **Figure 1.1**, in which Section 3 is further divided into 3 sub-sections: Section 3A, 3B and 3C. The construction of the project will be implemented in two phases – Phase 1 and Phase 2. Phase 1 covers Section 1, 2 and 4; Phase 2 covers Sections 3A and 3C.

An Environmental Permit (EP) covering the overall proposed works was issued in June 2009 (Permit No. EP-347/2009). An application for Variation of the Environmental Permit (VEP) (Application No. VEP-314/2010) was subsequently submitted on 24 May 2010 and the amended Environmental Permit (Permit No. EP-347/2009/A) was issued by EPD on 9 June 2010.

The Architectural Services Department (ArchSD) has been entrusted with the management of the Project by the Project Proponent – the Secretary for Security of the HKSAR Government. Mott MacDonald Hong Kong Limited (MMHK) has in turn been commissioned by ArchSD as the consulting engineer for the entire Project under Consultancy Agreement No. 9SN005, and is the Engineer’s Representative (ER) for construction of the Project.

In April 2015, ArchSD issued Works Order No. ASD011777 incorporating the improvement works for boundary fence at Mai Po, Lok Ma Chau and Sha Tau Kok for Phase 1, and Quotation Contract No. 002/15/PMB203 covering landscape works at Tak Yuet Lau for Phase 2 (referred to hereafter as the “subject works”) to Lanon Development Limited (LANON) and Wah On Garden Landscaping Limited (WAH ON) (“The Contractors”) respectively. MMHK and Ramboll Environ Hong Kong Limited (Ramboll Environ) have been commissioned as the ET and IEC respectively to undertake the Environmental Monitoring and Audit (EM&A) programme as described in the approved EM&A Manual of the Project.

# Construction of a Secondary Boundary Fence and New Sections of Primary Boundary Fence and Boundary Patrol Road

Improvement Works for Mai Po, Lok Ma Chau, Sha Tau Kok and Planting Works at Tak Yuet Lau – Monthly EM&A Report for September 2015



This monthly EM&A report summarises the environmental monitoring and audit works, list of activities and mitigation measures implemented for the subject works during the period of 1 to 30 September 2015 inclusive ('reporting month').

The scope of works for improvement works for boundary Fence at Mai Po, Lok Ma Chau and Sha Tau Kok consists of:

## *Mai Po Section:*

- Replacement of hinges at gate no. 102C, 102B, 102A, 101K, 101J, 101I, 101H, 99E, 99A, 98 (Total 10 nos.)
- Installation of additional CCTV information plates at Gate no. 99D, 99G, 100A, 100B, 100E, 100G, 101B, 101C, 101D, 101E, 101G (Total 11 nos.)
- Removal of existing vegetation and top soil and provision 75mm thick concrete slab on verge area between fence kerb and road kerb along SBF
- Modification of gate no. 101K including installation of additional horizontal support and 6 nos. additional heavy duty hydraulic wheels
- Removal of existing vegetation and top soil and construction concrete pavement at gate no. 100D and 100H
- Installation of EPDM gasket for 150X150 opening at the various gates
- Trimming down of existing pavement outside Pak Hok Chau Checkpoint and installation anti-slip tiles with same FFL with existing

## *Lok Ma Chau Section:*

- Replacement installed information plate at gate no. 78, 78B, 81A, 89A, 91A, 96A, 97 (Total 7 Nos.)
- Installation additional information plate for gate no. 91A and 91B
- Installation of 1 nos. proposed retractable awning of approx. size of 5m in width and 3m in projection of existing canopy at entrance of Tak Yuet Lau Police Post
- Installation of 8 nos. of "No climbing" warning signs on the railing at DSD Maintenance Road Behind Ng Tung River
- Construction of 4 nos. of "Fish Convex Mirror: and the associated installation works

## *Sha Tau Kok Section:*

- Installation of 2 nos. anti-mosquito lantern for booths of vehicular inspection shelter and 2 nos. anti-mosquito lantern for gate 1 checkpoint
- Installation of anti-slip tiles at vehicular inspection shelters
- Construction of ramp, handrail and stainless steel wire mesh guard at gate 1 checkpoint
- Installation of CCTV plates at gate M/P4-2, gate M/P4-7, gate besides waterfront, fence near CCTV post 26B in VHA, fence near CCTV post 20B in VHA, gate 6 at Shan Tsui Village and gate 7 at Shan Tsui Village
- Construction of additional lamp poles (Flood light) to replace the existing lamp
- Installation of additional information plates on pedestrian gate no. M/P4-7 and M/P4-2 at Sha Tau Kok
- Provision of FCA road marking at Sha Tau Kok
- Provision of portable lifting facilities for lifting submerge pump at Sha Tau Kok.

The scope of works for landscaping works at Tak Yuet Lau consists of:

- Site boundary setting-out
- Site clearance
- Import of soil mix
- Hydroseeding

216727/ENL/12/09/A October 2015

P:\Hong Kong\INF\Projects\216727-Boundary Fence\Environmental\Environmental Team\Phase 2\Deliverable\Monthly EM&A Report\2015-09\EM&A Report (Sep 2015) Rev A\_r2.doc

- Planting of trees
- Staking support the new planted tree
- Planting of shrubs
- Mulching

## **1.2 Project Organisation**

The organisation chart and lines of communication with respect to the on-site environmental management structure together with the contact information of the key personnel are shown in [Appendix B](#).

## **1.3 Works Undertaken in the Reporting Month**

The following activities have taken place during the reporting month:

### ***Improvement Works for Boundary Fence at Mai Po, Lok Ma Chau and Sha Tau Kok:***

- Removal existing vegetation and top soil and provision 75mm thick concrete slab on verge area between fence kerb and road kerb along SBF

### ***Landscaping Work at Tak Yuet Lau:***

- Tree planting
- Shrub planting
- Hydro seedling

## 2. EM&A Requirements

### 2.1 Summary of EM&A Requirements

The EM&A programme requires environmental monitoring of construction noise as well as environmental site inspections for air quality, noise, water quality, waste management, ecology, landscape and visual, as specified in the approved EM&A Manual.

Originally, the EM&A Manual designated five locations as noise monitoring stations during the construction phase for Section 1, 2 and 4. However, noise levels at only one of these monitoring stations (as shown in **Table 2.1.**) was monitored during the reporting month. The reasons for this arrangement are detailed in Section 3.2.

A summary of impact EM&A requirements is presented in **Table 2.1.** The Environmental Quality Performance Limits and the Event and Action Plans (for construction noise only) are shown in **Appendix C** and **Appendix D** respectively.

Table 2.1: Summary of EM&A Impact Requirements

Parameters	Description	Location(s)	Frequency	Duration
Air	On-site Inspection	Active Works Sites	Weekly	During Construction
Noise	L <sub>eq</sub> , 30min	VH03	Weekly	During Construction
Waste management	On-site Waste Audit	Active Works Sites	Weekly	During Construction
	On-site Waste Inspection			
Wastewater	On-site Wastewater Audit	Active Works Sites	Weekly	During Construction
Ecology	On-site Audit of Recommended Ecological Mitigation Measures	Active Works Sites	Periodically (by Contractor)	As specified in EM&A Manual (see Table E.5)
Landscape and Visual	On-site Audit of Recommended Landscape and Visual Mitigation Measures	Active Works Areas	Regular intervals (by Contractor/ Landscape Sub-Contractor)	As specified in EM&A Manual (see Table E.6)
General Site Conditions	Environmental Site Inspection	Works areas and areas affected by works	Weekly	During Construction

### 2.2 Implementation of Environmental Mitigation Measures

The Contractor is required to implement mitigation measures listed in the latest valid EP and FEP(s) (where applicable), EIA Report and EM&A Manual. During routine site inspections, the Contractor's implementation of mitigation measures, if any, are to be inspected and reviewed. A schedule of the implementation of mitigation measures identified at the EIA stage is given in **Appendix E.**

## 3. Noise Impact Monitoring

### 3.1 Monitoring Parameters, Frequency and Duration

Following the requirements in the EM&A Manual for noise, noise monitoring has to be carried out during the construction phase. Continuous noise monitoring for the A-weighted levels  $L_{eq}$ ,  $L_{10}$  and  $L_{90}$  is undertaken once per every week during daytime hours (between 07:00 and 19:00) on normal weekdays.

As the topsoil removal work of improvement work commenced in mid-September 2015, the first noise impact monitoring for the improvement work was conducted on 18 September 2015.

**Table 3.1** summarizes the monitoring parameters, frequency and duration of noise monitoring. The noise monitoring schedule during the reporting month is presented in **Appendix F**.

Table 3.1: Noise Monitoring Parameters, Frequency and Duration

Monitoring Station	Parameters	Frequency	Duration
VH03	$L_{eq}$ , $L_{90}$ & $L_{10}$	Once every week	30 min

### 3.2 Monitoring Location

Originally, five construction noise monitoring stations were proposed in the EM&A Manual for Section 1, 2 and 4, namely: VH01 (Village House at Mai Po), VH03 (Village House at Mai Po), MTL01 (Village House at Ma Tso Lung), STK03 (Block 1, Sha Tau Kok Estate) and STK05 (Village House at Sha Tau Kok).

For Section 1, 2 and 4, as the major construction of constructing the fencing has been conducted in earlier stages of Phase 1, the improvement works as mentioned in Section 1.1 are minor works unlikely to produce significant impact on the NSRs, except for the construction of concrete pavement in Section 1. With regard to the nature of the subject works, only VH03 is proposed as a noise impact monitoring station.

STK03 was mainly selected for the construction works related to the SBF and the new checkpoint and kiosk/guard house in Sha Tau Kok, while STK05 was mainly selected for the removal of the existing checkpoint at Shek Chung Au.

However, access to STK03 to perform noise monitoring was not granted, therefore an alternative nearby location – STK-DBD (HKPF Operation Base, Sha Tau Kok Division, Border District) – was proposed by ET and agreed to by IEC and EPD. Baseline and impact noise monitoring was conducted at STK-DBD from 16 to 29 March 2010 and from June 2010 to January 2012 respectively.

Currently, the commencement date of demolition works at the existing checkpoint at Shek Chung Au is subject to confirmation. Baseline monitoring at STK05 was conducted from 7 to 20 September 2012. No impact noise monitoring at STK05 has been carried out at this stage.

As a result, only one noise impact monitoring station is included in the current EM&A programme for the subject works during the reporting period. The location of the agreed noise quality monitoring station is listed in **Table 3.2** and shown in **Figure 2.1**.

Table 3.2: Noise Impact Monitoring Location

Monitoring Station	Description of Location	Type of measurement
VH03	Village House at Mai Po	Façade

### 3.3 Monitoring Equipment

Integrating Sound Level Meter will be used for noise monitoring. It is a Type 1 sound level meter capable of giving a continuous readout of the noise level readings including equivalent continuous sound pressure level ( $L_{eq}$ ) and percentile sound pressure level ( $L_x$ ). They comply with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). **Table 3.3** summarizes the typical noise monitoring equipment used.

Table 3.3: Noise Monitoring Equipment

Equipment	Model
Integrating Sound Level Meter	Rion NL-52
Acoustic Calibrator	Rion NC-73

### 3.4 Equipment Calibration

The calibration frequencies of the monitoring equipment are provided in **Table 3.4**.

Table 3.4: Noise Monitoring Equipment Calibration Frequencies

Equipment, Model and Serial Number	Calibration Frequency
Integrating Sound Level Meter	Every year
Acoustic Calibrator	Every year

The noise monitoring equipment calibration certificates are presented **Appendix G** in this report.

### 3.5 Monitoring Methodology

#### 3.5.1 Field Monitoring

- The Sound Level Meter was set on a tripod at a height of at least 1.2 m above the ground.
- Façade measurements were made at the monitoring locations.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
  - frequency weighting: A
  - time weighting: Fast
  - time measurement: 5-minute intervals (between 07:00 and 19:00);  $L_{eq}$  (30 min) was determined by calculating the logarithmic average of six  $L_{eq}$  (5-min) data.
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1 kHz. If the difference in the calibration level before and after measurement was more than 1 dB, the measurement would be considered invalid and have to be repeated after re-calibration or repair of the equipment.
- During the monitoring period, the  $L_{eq}$ ,  $L_{10}$  and  $L_{90}$  noise levels were recorded. In addition, any site observations and noise sources were recorded on a standard record sheet.



### 3.5.2 Maintenance and Calibration

- The microphone head of the sound level meter and calibrator is cleaned with soft cloth at quarterly intervals.
- The meter and calibrator are sent to the supplier or Hong Kong Laboratory Accreditation Scheme (HOKLAS) laboratory to check and calibrate at yearly intervals.

## 3.6 Results of Impact Monitoring

Noise impact monitoring were conducted on 18, 23 and 30 September 2015 during the reporting month.

The measured construction noise level, in terms of  $L_{eq}$  (30-min), during the reporting month are summarised in **Table 3.5**.

Table 3.5: Result of Noise Impact Monitoring

Monitoring Station	Measured $L_{eq}$ (30-mins) Range, dB(A)	Limit Level for $L_{eq}$ , dB(A)
VH03	45-61	75

No exceedance of Action / Limit Levels for construction noise was recorded.

The graphical presentations of the measured construction noise level of the reporting month of noise impact monitoring are presented in [Appendix H](#). The general weather conditions and graphical presentation are presented in **Appendix K**.

## 4. Environmental Site Inspection and Audit

### 4.1 Site Inspections

Environmental site inspections were carried out on a weekly basis to monitor the proper implementation of environmental pollution control and mitigation measures for the subject works. In the reporting month, one monthly site inspection was carried out jointly by the ER, Contractor, ET and IEC on 23 September 2015. Weekly site inspections were carried out by ET on 4, 9, 18, 23 and 30 September 2015. The EM&A schedule is presented in **Appendix F**.

Major findings provided by ET during the weekly site inspections are summarised in **Table 4.1**. In general, the works site areas were found to be in compliance with the environmental mitigation requirements listed in the EM&A Manual and no adverse impacts were found.

Table 4.1: Summary of Environmental Site Inspections

Date of Inspection	Major Observations	Status
4 Sep 2015	No major observations.	-
9 Sep 2015	No major observations.	-
18 Sep 2015	No major observations.	-
23 Sep 2015	No major observations.	-
30 Sep 2015	Topsoil removal for pavement work at Section 1 was observed. The Contractor was reminded to clear the removed topsoil properly as soon as possible.	Clearance of the removed topsoil was observed. (closed) (7 Oct 2015)
	Uncovered removed soil on the patrol road side of Section 1 was observed. The Contractor was reminded to provide waterproof covering to prevent site runoff and dust emission.	No uncovered soil on the patrol road side was observed for the finished section. (closed) (7 Oct 2015)

### 4.2 Environmental Meetings

No environmental meeting was held during the reporting month.

### 4.3 Status of Environmental Submissions, Permits and Licences

A summary of status of all environmental submissions, valid permits/licences, and/or notifications to EPD for this Project during the reporting month is presented in **Table 4.2**.

Table 4.2: Status of Environmental Permits and Licences

Statutory Reference	Description	Permit / Reference No.	Status
EIAO	Environmental Permit	EP-347/2009/A	Valid
WDO	Bill Account Disposal	7021313	Valid

Legend: EIAO – Environmental Impact Assessment Ordinance  
WDO – Waste Disposal Ordinance

Note: The Bill Account Disposal for Contract No. TCC508 was registered by the Lanon Development Limited.

#### **4.4 Advice on the Solid and Liquid Waste Management Status**

The construction and demolition (C&D) material and general refuse generated by the subject works of the Project in the reporting month are shown in **Appendix I**. Wastes were handled and disposed from site in accordance with the EM&A Manual and all relevant legislation and regulations.

#### **4.5 Review of Environmental Monitoring Procedures**

The monitoring works conducted by the Environmental Team have been reviewed regularly. No changes in the environmental monitoring procedures are considered necessary at this stage.

#### **4.6 Implementation Status of Environmental Mitigation Measures**

An Implementation Schedule of Mitigation Measures from the EIA Report / EM&A Manual is provided in **Appendix E**, in the following order (see **Table 4.3**):

Table 4.3: Implementation Schedule of Mitigation Measures

<b>Parameter</b>	<b>Table</b>	<b>Parameter</b>	<b>Table</b>
Air Quality	Table E.1	Waste Management	Table E.4
Noise	Table E.2	Ecology	Table E.5
Water Quality	Table E.3	Landscape and Visual	Table E.6

## 5. Record of Non-compliance, Complaints, Notifications of Summons and Successful Prosecutions

### 5.1 Non-compliance of Action and Limit Levels

There was no breach of Action or Limit Levels for construction noise impact monitoring in the reporting month.

### 5.2 Environmental Complaints

No environmental complaints were received or made against the subject works of the Project during the reporting month. The complaint log is presented in Appendix J.

### 5.3 Notifications of Summons and Successful Prosecutions

No notifications of summons or successful prosecution were received or made against the subject works of the Project during the reporting month.

## 6. Future Key Issues

### 6.1 Construction Programme for the Next Reporting Month

The major construction works are forecast for the subject works in October 2015 will include;

#### ***Improvement Works for Boundary Fence at Mai Po, Lok Ma Chau and Sha Tau Kok***

- Removal existing vegetation and top soil and construction concrete pavement in Section 1.

#### ***Landscaping Works at TakYuet Lau***

- Tree planting and shrub planting.

### 6.2 Key Issues for the Next Reporting Month

Future key issues to be considered in the forthcoming month include:

#### ***Air***

- Regular maintenance of all plant and equipment;
- Handling of any excavated dusty materials or stockpile of dusty material; and
- Spraying of water prior to any loading, unloading or transfer of dusty materials.

#### ***Noise***

- Location of noisy equipment and noisy activities relative to the Noise Sensitive Receivers (NSRs);
- Avoiding the operation of unused equipment, and minimising the use of Powered Mechanical Equipment (PME) and parallel use of noisy equipment / machinery; and
- Regular maintenance of all plant and equipment.

#### ***Water Quality***

- No discharge of silty water into the storm drain and drainage channel within and the vicinity of the site;
- Removal off-site of construction plant causing pollution to water system due to leakage of oil or fuel; and
- Temporary stockpiling of excavated soil in a specially designated area with provision of tarpaulin cover.

#### ***Waste***

- Control measures at the stockpiling area to prevent the generation of dust and pollution of stormwater channels, fish ponds or river channels;
- Segregation, storage, transportation and disposal of different types of waste; and
- Keeping of records of quantities of wastes generated, recycled and disposal (with locations).

#### ***Ecology***

- Good site practices for controlling the dust and water quality; and
- Clear definition of works limit to avoid impact on adjacent habitats.

#### ***Landscape and Visual***

- Retain tree with high amenity or ecology value and contributing most to landscape and amenity of site;
- Precautionary area around trees to be retained equal to half of the tree canopy diameter;

216727/ENL/12/09/A October 2015

P:\Hong Kong\INF\Projects2\216727-Boundary Fence\Environmental\Environmental Team\Phase 2\Deliverable\Monthly EM&A Report\2015-09\EM&A Report (Sep 2015) Rev A\_r2.doc

- Prohibition of the storage of materials including fuel, the movement of construction vehicles, and the refuelling and washing of equipment including concrete mixers within the precautionary area;
- Pruning of the branches of existing trees identified for transplantation and retention;
- Rectification and repair of damaged vegetation following the construction phase to its original condition;
- Careful monitoring of all works affecting the trees identified for retention and transplantation; and
- Enforcement of construction site controls including storage of materials, location and appearance of site accommodation and the careful design of site lighting to prevent light spillage.

Environmental mitigation measures will be implemented on site as recommended and weekly site audits will be carried out to ensure that the environmental conditions are acceptable.

### **6.3 Monitoring Schedule for the Next Reporting Month**

The tentative schedule for environmental site inspection and construction noise monitoring in October 2015 is provided in **Appendix F**. Actual dates may change due to unforeseen events such as inclement weather.

## 7. Conclusions and Recommendations

### 7.1 Conclusions

The construction phase EM&A programme for the subject works was performed from 1 to 30 September 2015 during which improvement works for the boundary fence at Mai Po and landscaping works at Tak Yuet Lau were conducted. All monitoring and audit results and findings in the reporting month were checked and reviewed.

Weekly construction noise monitoring was carried out in the reporting month (from 18 September 2015 onwards). No exceedance of the noise Limit Level was recorded. Furthermore, no noise-related complaint was received or followed-up by ET during the reporting month, therefore no Action Level exceedance was recorded.

Environmental site inspections were carried out four times during the reporting month. During the site audits, recommendations on remedial actions were given to the Contractor for any deficiencies identified.

Wastes were handled and disposed from site in accordance with EM&A Manual and all relevant legislation and regulations.

There were no compliance issues involving wastes in accordance with the EM&A Manual and all relevant legislation and regulations.

No environmental complaints, notification of summons of successful prosecutions were received or made against the subject works of the Project during the reporting month.

Overall, the EM&A programme for the subject works during the reporting month was in compliance with the relevant EIA Report, EM&A Manual, EP and FEP(s) and all relevant legislation and regulations.


### 7.2 Recommendations

Improvements in the implementation of mitigation measures with respect to air quality, water quality and waste management were recommended based on the deficiencies identified during environmental site audits in the reporting month. No further recommendations were made at this stage pending more site progress achieved.



圖例：  
LEGEND:

- 建議於現有邊界巡邏通路興建的輔助邊界圍網  
PROPOSED SECONDARY BOUNDARY FENCE  
ALONG EXISTING BOUNDARY PATROL ROAD
- 建議的主要及輔助邊界圍網及新邊界巡邏通路  
PROPOSED NEW BOUNDARY PATROL ROAD WITH  
PRIMARY AND SECONDARY BOUNDARY FENCES
- 擬將移除的現有邊界圍網  
EXISTING BOUNDARY FENCE TO BE REMOVED

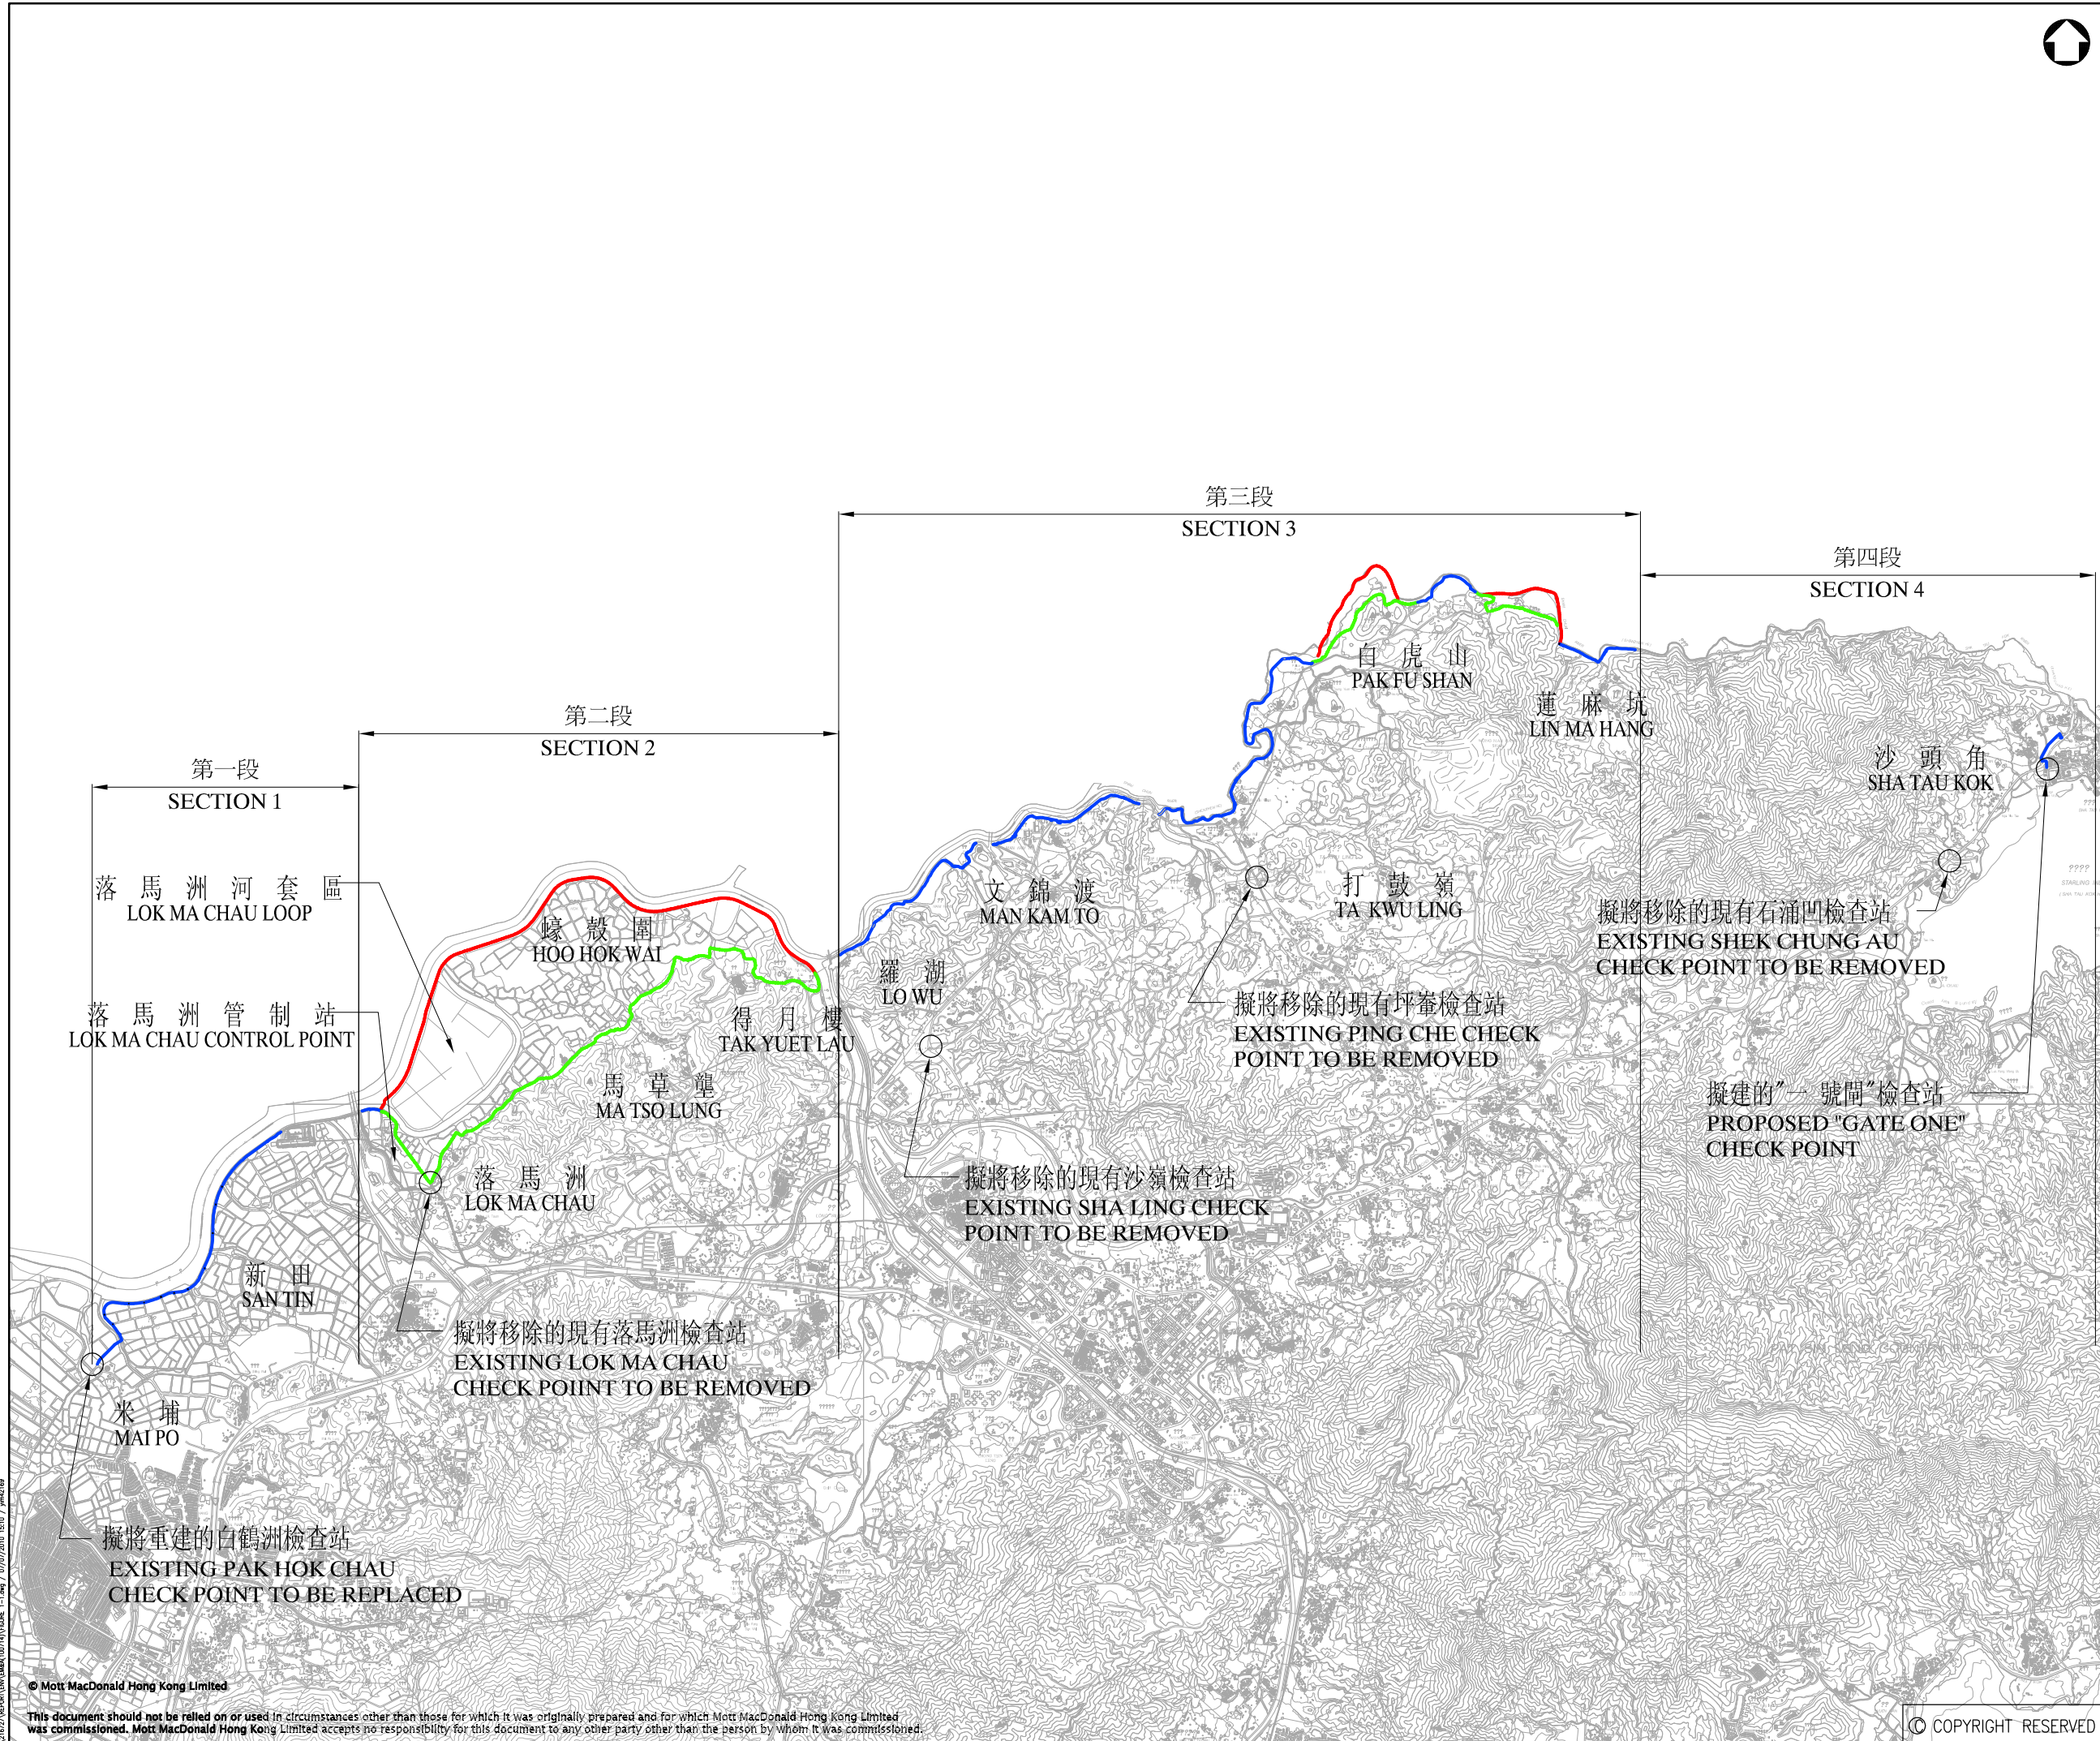

P1	JUL 10	AT	FIRST ISSUE	BW	TI
Rev	Date	Drawn	Description	Ch'k'd	App'd

Client



ARCHITECTURAL  
SERVICES  
DEPARTMENT




20/F Two Landmark East  
100 Hoi King Street  
Kowloon, Hong Kong  
T +852 2828 8707  
F +852 2827 1823  
W www.mottmac.com.hk

Project  
CONSTRUCTION OF A SECONDARY  
BOUNDARY FENCE AND NEW SECTIONS  
OF PRIMARY BOUNDARY FENCE  
AND BOUNDARY PATROL ROAD

Title  
概覽圖  
GENERAL LAYOUT PLAN

Designed	WHC	Eng.Chk.	WHC	
Drawn	MCL	Coordination	WHC	
Dwg.Chk.	WHC	Approved	TI	
Scale	Project 216727		Status	
	N.T.S.		CAD File	INF
Drawing No.	216727/REPORT/DWG/DM&A(100714)/FIGURE 1-1.dwg		Rev	
	FIGURE 1.1 (圖 1.1)		P1	



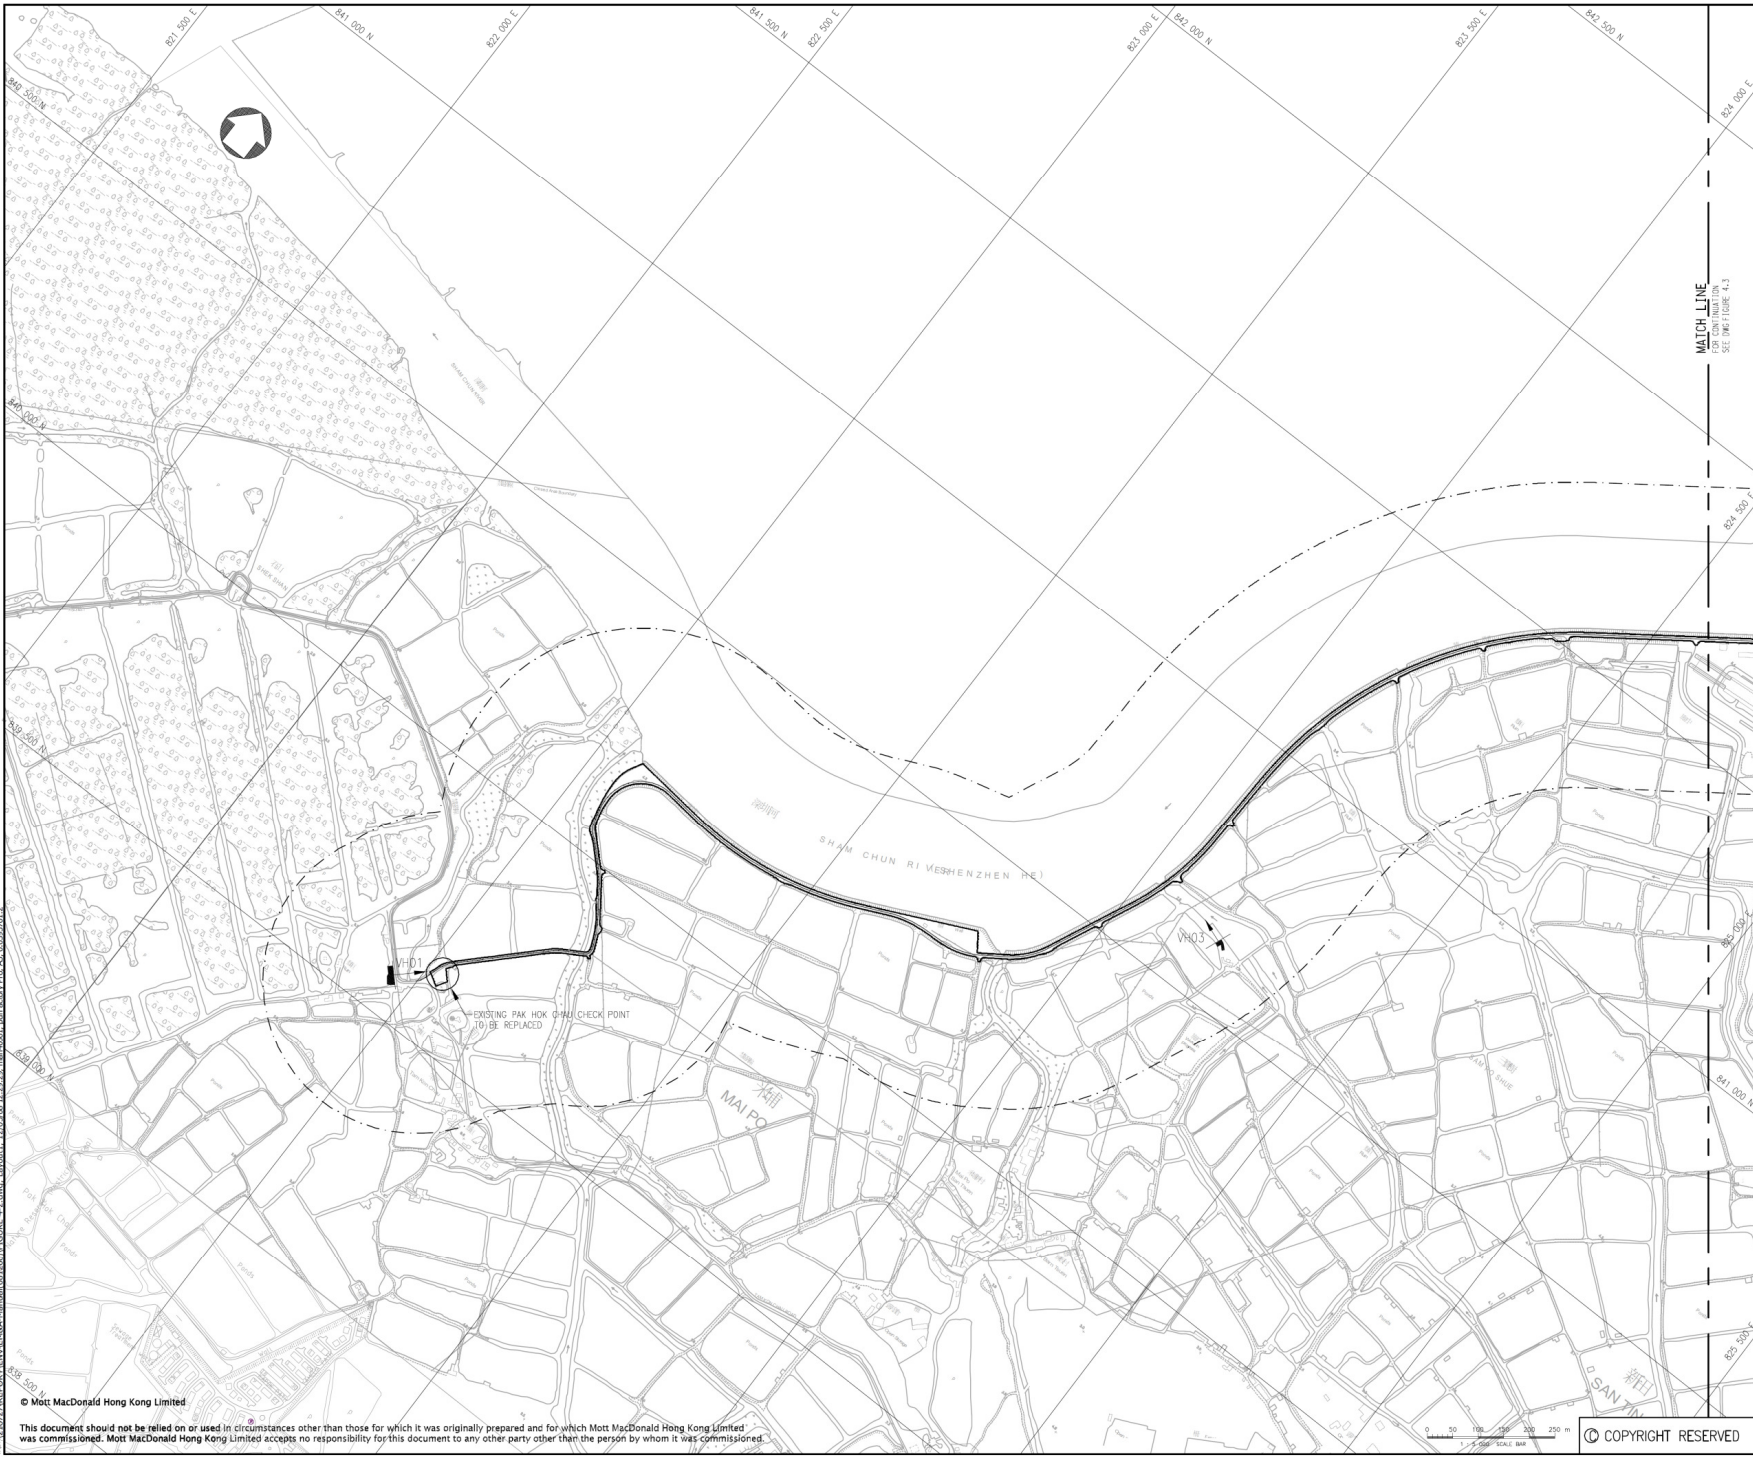

LEGEND :

- 300m ASSESSMENT AREA
- NOISE SENSITIVE RECEIVER
- FACADE FACING

P2	DEC 08	MING	FORMAL SUBMISSION	BL	AFK
P1	NOV 08	MING	ISSUE FOR COMMENT	BL	AFK
Rev	Date	Drawn	Description	Chk'd	App'd



Mott MacDonald Hong Kong Ltd  
 7th Floor  
 West Wing Office Building  
 New World Centre  
 27 Salisbury Road  
 Tsim Sha Tsui, Kowloon  
 Hong Kong  
 Tel: 2828 5737  
 Fax: 2827 1823  
 Web: www.mottmac.com.hk

Project  
**CONSTRUCTION OF A SECONDARY BOUNDARY FENCE AND NEW SECTIONS OF PRIMARY BOUNDARY FENCE AND BOUNDARY PATROL ROAD**

Title  
**LOCATION OF NOISE MONITORING STATIONS**

Designed	BL	Eng. Chk.	WHC
Drawn	MING	Coordination	WHC
Eng. Chk.	BL	Approved	AFK
Scale	1 : 5000@A1	Project	216727
Rev		CAD File	

Drawing No. **FIGURE 2.1** Rev. **P2**

C:\p2\216727\216727-001\216727-001.dwg, Layout1, 2010/08/22 10:50:51, m000501, mottmac.com.hk, 0.00001012

© Mott MacDonald Hong Kong Limited

This document should not be relied on or used in circumstances other than those for which it was originally prepared and for which Mott MacDonald Hong Kong Limited was commissioned. Mott MacDonald Hong Kong Limited accepts no responsibility for this document to any other party other than the person by whom it was commissioned.



© COPYRIGHT RESERVED

# Appendices










Appendix A. Construction Works Programme _____	15
Appendix B. Project Organisation Chart _____	16
Appendix C. Environmental Quality Performance Limits _____	17
Appendix D. Event and Action Plans _____	18
Appendix E. Schedule of Mitigation Measures from the EIA Report and EM&A Manual _____	19
Appendix F. EM&A Schedule _____	30
Appendix G. Calibration Certificates _____	32
Appendix H. Noise Monitoring Results and Graphical Presentation _____	33
Appendix I. Monthly Waste Flow Table _____	34
Appendix J. Complaint Log _____	37
Appendix K. Weather Information from Hong Kong Observatory _____	38

# Appendix A. Construction Works Programme

**Contract NO. 002/15/PMB203**

**Landscaping Works at Tak Yuet Lau for Construction of a Secondary Boundary Fence and New Sections of Primary Boundary Fence and Boundary Patrol Road (Phase 2) (Programme No. 12GB)**


**Working Programme**

	17/8-22/8	24/8-29/8	31/8-5/9
<b>YEAR 2015</b>	Week 20	Week 21	Week 22
<b>DESCRIPTION</b>			
Import of soil mix			
Setiing out			
Hydroseeding			
Planting of trees			
Staking support the new planted tree			
Start Tree Monitoring			
Planting of shrubs			
Mulching			
Dress up the site			
Completion of Maintenance period	24 Months after Issuance of Completion Certificate		



ID	Task Name	Duration	Start	Finish	Gantt Chart											
					2nd Quarter			3rd Quarter			4th Quarter					
					A	M	J	J	A	S	O	N				
1	<b>Works Order Period (Improvement Works for Boundary Fence at Mai Po, Lok Ma Chau and Sha Tau Kok)</b>	<b>184 days</b>	<b>Tue 28/4/15</b>	<b>Wed 28/10/15</b>	28/4 ————— 28/10											
2	<b>Works Order Commcement Date</b>	<b>0 days</b>	<b>Tue 28/4/15</b>	<b>Tue 28/4/15</b>	◆ 28/4											
3	<b>Mai Po Section</b>	<b>184 days</b>	<b>Tue 28/4/15</b>	<b>Wed 28/10/15</b>	28/4 ————— 28/10											
4	<b>1.) Replacement of Hinge at Gate no. 102C, 102B, 102A, 101K, 101J, 101I, 101H, 99E, 99A, 98 (Total 10 Nos.)</b>	<b>164 days</b>	<b>Tue 28/4/15</b>	<b>Thu 8/10/15</b>	—————											
5	Material Procurement and Fabrication	104 days	Tue 28/4/15	Sun 9/8/15	—————											
6	Replacement of Hinge	60 days	Mon 10/8/15	Thu 8/10/15	—————											
7	<b>2.) Installation Additional CCTV Information Plates at Gate no. 99D, 99G, 100A, 100B, 100E, 100G, 101B, 101C, 101D, 101E, 101G (Toal 11 Nos.)</b>	<b>127 days</b>	<b>Tue 28/4/15</b>	<b>Tue 1/9/15</b>	—————											
8	Material Submission, Procurement and Fabrication	99 days	Tue 28/4/15	Tue 4/8/15	—————											
9	Installation of CCTV Information Plates	28 days	Wed 5/8/15	Tue 1/9/15	—————											
10	<b>3.) Provision of Speed Limit Road Marking at Various Locations as Specified in the Drawings (Details to be Issued)</b>	<b>70 days</b>	<b>Mon 6/7/15</b>	<b>Sun 13/9/15</b>	—————											
11	Material Submission	60 days	Mon 6/7/15	Thu 3/9/15	—————											
12	Provision FCA Road Marking	10 days	Fri 4/9/15	Sun 13/9/15	—————											
13	<b>4.) Removal Existing Vegetation and Top Soil and Provision 75mm Thick Concrete Slab on Verge Area between Fence Kerb and Road Kerb along SBF</b>	<b>160 days</b>	<b>Tue 28/4/15</b>	<b>Sun 4/10/15</b>	—————											
14	Application of Excavation Permit and Lead Time Waiver*	100 days	Tue 28/4/15	Wed 5/8/15	—————											
15	Construction of Concrete Slab on Verge Area	60 days	Thu 6/8/15	Sun 4/10/15	—————											
16	<b>5.) Modification Gate no. 101K including Installation of Additional Horizontal Support and 6 nos. Additional Heavy Duty Hydraulic wheels</b>	<b>184 days</b>	<b>Tue 28/4/15</b>	<b>Wed 28/10/15</b>	—————											
17	Material Submission, Procurement and Fabrication	100 days	Tue 28/4/15	Wed 5/8/15	—————											
18	Modification of Gate	20 days	Fri 9/10/15	Wed 28/10/15	—————											
19	<b>6.) Removal Existing Vegetation and Top Soil and Construction Concrete Pavement at Gate no. 100D and 100H</b>	<b>174 days</b>	<b>Tue 28/4/15</b>	<b>Sun 18/10/15</b>	—————											
20	Application of Excavation Permit and Lead Time Waiver	100 days	Tue 28/4/15	Wed 5/8/15	—————											
21	Detection Survey of Underground Utilities	2 days	Sat 3/10/15	Sun 4/10/15	—————											
22	Construction of Concrete Pavement	14 days	Mon 5/10/15	Sun 18/10/15	—————											
23	<b>7.) Removal Existing Vegetation and Top Soil and Construction Concrete Pavement Run-in at Gate no. 100D and 100H</b>	<b>184 days</b>	<b>Tue 28/4/15</b>	<b>Wed 28/10/15</b>	—————											
24	Application of Excavation Permit and Lead Time Waiver	100 days	Tue 28/4/15	Wed 5/8/15	—————											
25	Detection Survey of Underground Utilities	2 days	Sat 17/10/15	Sun 18/10/15	—————											
26	Construction of Concrete Pavement Run-in	10 days	Mon 19/10/15	Wed 28/10/15	—————											
27	8.) Installation of EPDM Gasket for 150x150 Opening at the Various Gates as per Sketch no. SK009	7 days	Mon 17/8/15	Sun 23/8/15	—————											
28	<b>9.) Trimming Down Existing Pavement outside Pak Hok Chau Checkpoint and Installation Anti-slip Tiles with same FFL with Existing</b>	<b>44 days</b>	<b>Tue 15/9/15</b>	<b>Wed 28/10/15</b>	—————											
29	Material Submission and Procurement	14 days	Tue 15/9/15	Mon 28/9/15	—————											
30	Trimming Down Existing Pavement and Installation of Anti-slip Tiles	30 days	Tue 29/9/15	Wed 28/10/15	—————											
31	<b>Lok Ma Chau Section</b>	<b>184 days</b>	<b>Tue 28/4/15</b>	<b>Wed 28/10/15</b>	28/4 ————— 28/10											
32	<b>10.) Replacement Installed Information Plate at Gate no. 78, 78B, 81A, 89A, 91A, 96A, 97 as per Sketch no. SK046 (Total 7 Nos.)</b>	<b>141 days</b>	<b>Tue 28/4/15</b>	<b>Tue 15/9/15</b>	—————											
33	Material Submission, Procurement and Fabrication	91 days	Tue 28/4/15	Mon 27/7/15	—————											
34	Installation of Information Plates	14 days	Wed 2/9/15	Tue 15/9/15	—————											
35	<b>11.) Installation Additional Information Plate for Gate no. 91A and 91B as per Sketch no. SK047-048</b>	<b>146 days</b>	<b>Tue 28/4/15</b>	<b>Sun 20/9/15</b>	—————											
36	Material Submission, Procurement and Fabrication	91 days	Tue 28/4/15	Mon 27/7/15	—————											
37	Installation of Information Plates	5 days	Wed 16/9/15	Sun 20/9/15	—————											

ID	Task Name	Duration	Start	Finish	2nd Quarter			3rd Quarter			4th Quarter				
					A	M	J	J	A	S	O	N			
38	<b>12.) Installation 1 nos. Proposed Retractable Awning of approx. Size of 5m in width and 3m in Projection for Existing Canopy at Entrance of Tak Yuet Lau Police Post</b>	<b>114 days</b>	<b>Tue 28/4/15</b>	<b>Wed 19/8/15</b>											
39	Material Submission, Procurement and Fabrication	100 days	Tue 28/4/15	Wed 5/8/15											
40	Installation of Proposed Retractable Awning	14 days	Thu 6/8/15	Wed 19/8/15											
41	<b>13.) Installation 8 nos. of "No Climbing" Warning Signs on the Railing at DSD Maintenance Road Behind Ng Tung River</b>	<b>164 days</b>	<b>Tue 28/4/15</b>	<b>Thu 8/10/15</b>											
42	Material Submission, Procurement and Fabrication	91 days	Tue 28/4/15	Mon 27/7/15											
43	Installation of Warning Signs	18 days	Mon 21/9/15	Thu 8/10/15											
44	<b>14.) Construction 4 nos. of "Fish Convex Mirror" and the Associated Installation Works as per Sketch nos. SK052-054</b>	<b>184 days</b>	<b>Tue 28/4/15</b>	<b>Wed 28/10/15</b>											
45	Application of Excavation Permit	100 days	Tue 28/4/15	Wed 5/8/15											
46	Material Submission, Procurement and Fabrication	30 days	Tue 7/7/15	Wed 5/8/15											
47	Detection Survey of Underground Utilities	2 days	Thu 6/8/15	Fri 7/8/15											
48	Installation of "Fish Convex Mirror" and Associated Installation Works	82 days	Sat 8/8/15	Wed 28/10/15											
49	<b>Sha Tau Kok Section</b>	<b>184 days</b>	<b>Tue 28/4/15</b>	<b>Wed 28/10/15</b>											
50	<b>15.) Installation of 2 nos. Anti-mosquito Lantern for Booths of Vehicular Inspection Shelter and 2 nos. Anti-mosquito Lantern for Gate 1 Checkpoint G/F</b>	<b>114 days</b>	<b>Tue 28/4/15</b>	<b>Wed 19/8/15</b>											
51	Material Submission, Procurement and Fabrication	100 days	Tue 28/4/15	Wed 5/8/15											
52	Installation of Anti-mosquito Lantern	14 days	Thu 6/8/15	Wed 19/8/15											
53	<b>16.) Installation of Anti-slip Tiles at Vehicular Inspection Shelters</b>	<b>182 days</b>	<b>Tue 28/4/15</b>	<b>Mon 26/10/15</b>											
54	Application of Excavation Permit	150 days	Tue 28/4/15	Thu 24/9/15											
55	Detection Survey of Underground Utilities	2 days	Fri 25/9/15	Sat 26/9/15											
56	Material Submission, Procurement and Fabrication	40 days	Thu 9/7/15	Mon 17/8/15											
57	Installation of Anti-slip Tiles	30 days	Sun 27/9/15	Mon 26/10/15											
58	<b>17.) Construction Ramp, Handrail and Stainless Steel Wire Mesh Guard at Gate 1 Checkpoint</b>	<b>72 days</b>	<b>Tue 18/8/15</b>	<b>Wed 28/10/15</b>											
59	Consent for Construction at Gate 1 Check Point from HKPF & C&ED	30 days	Tue 18/8/15	Wed 16/9/15											
60	Detection Survey of Underground Utilities	2 days	Thu 17/9/15	Fri 18/9/15											
61	Material Submission, Procurement and Fabrication	30 days	Thu 20/8/15	Fri 18/9/15											
62	Construction Ramp, Handrail and Stainless Steel Wire Mesh Guard	40 days	Sat 19/9/15	Wed 28/10/15											
63	<b>18.) Installation CCTV Plates at Gate M/P4-2, Gate M/P4-7, Gate besides Waterfront, Fence near CCTV Post 26B in VHA, Fence near CCTV Post 20B in VHA, Gate 6 at Shan Tsui Village and Gate 7 at Shan Tsui Village</b>	<b>182 days</b>	<b>Tue 28/4/15</b>	<b>Mon 26/10/15</b>											
64	Material Submission, Procurement and Fabrication	91 days	Tue 28/4/15	Mon 27/7/15											
65	Installation of CCTV Plates	18 days	Fri 9/10/15	Mon 26/10/15											
66	<b>19.) Construction Additional Lamp Poles (Flood Light) to Replace the Existing Lamp as per Sketch no. SK017, 018A and 018B</b>	<b>184 days</b>	<b>Tue 28/4/15</b>	<b>Wed 28/10/15</b>											
67	Application of Excavation Permit	130 days	Tue 28/4/15	Fri 4/9/15											
68	Material Submission, Procurement and Fabrication	100 days	Tue 28/4/15	Wed 5/8/15											
69	Construction Additional Lamp Poles	50 days	Sat 5/9/15	Sat 24/10/15											
70	Testing & Commissioning	4 days	Sun 25/10/15	Wed 28/10/15											
71	<b>20.) Installation Additional Information Plates on Pedestrian Gate no. M/P4-7 and M/P4-2 at Sha Tau Kok</b>	<b>141 days</b>	<b>Tue 28/4/15</b>	<b>Tue 15/9/15</b>											
72	Material Submission, Procurement and Fabrication	91 days	Tue 28/4/15	Mon 27/7/15											
73	Installation of Information Plates	10 days	Sun 6/9/15	Tue 15/9/15											
74	<b>21.) Provision FCA Road Marking at Sha Tau Kok</b>	<b>71 days</b>	<b>Mon 6/7/15</b>	<b>Mon 14/9/15</b>											
75	Material Submission	60 days	Mon 6/7/15	Thu 3/9/15											
76	Provision FCA Road Marking	1 day	Mon 14/9/15	Mon 14/9/15											
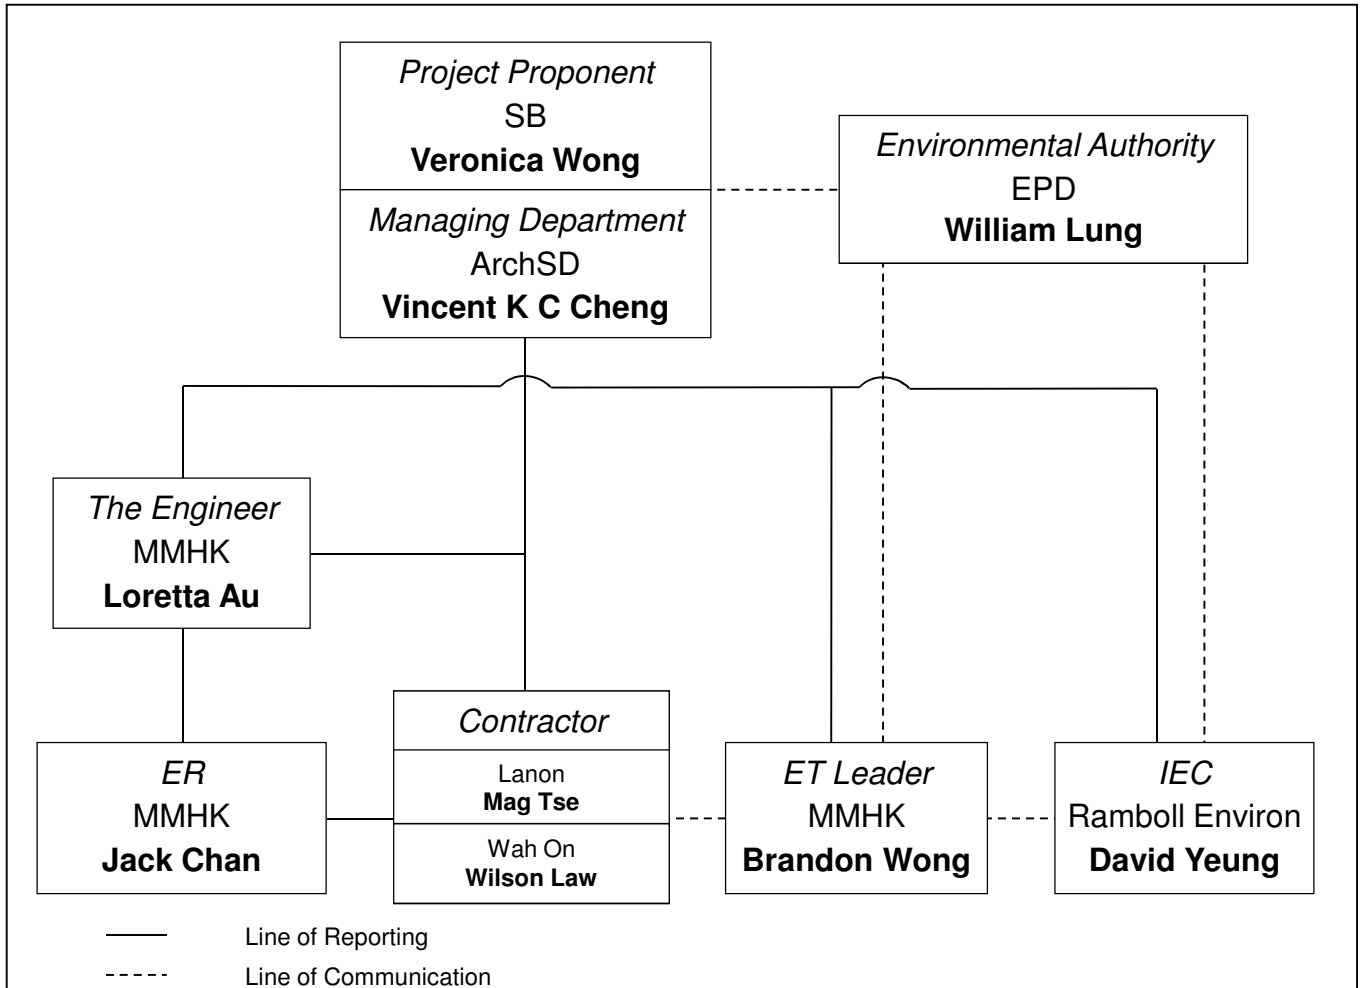
## Appendix B. Project Organisation Chart



Key Personnel Contact List			
Role	Department / Company	Name	Telephone No.
Project Proponent	Security Bureau (SB)	Ms. Veronica Wong	2810 3523
Managing Department	Architectural Services Department (ArchSD)	Mr. Vincent K C Cheng	2867 3871
Environmental Authority	Environmental Protection Department (EPD)	Mr. William Lung	2835 1065
The Engineer	Mott MacDonald Hong Kong Limited (MMHK)	Ms. Loretta Au	2828 5807
Engineer's Representative (ER)	Mott MacDonald Hong Kong Limited (MMHK)	Mr. Jack Chan	9837 7443
Independent Environmental Checker (IEC)	Ramboll Environ Hong Kong Limited (Ramboll Environ)	Mr. David Yeung	3465 2888
Environmental Team (ET) Leader	Mott MacDonald Hong Kong Limited (MMHK)	Mr. Brandon Wong	2828 5875
The Contractor / Project Manager	Lanon Development Limited (Lanon)	Mr. Mag Tse	9161 4727
The Contractor / Project Manager	Wah On Garden Landscaping Limited (Wah On)	Mr. Wilson Law	9046 6205

 Architectural Services Department	 Mott MacDonald	<b>Construction of a Secondary Boundary Fence and New Sections of Primary Boundary Fence and Boundary Patrol Road</b> Phase 2 – Improvement Works for Boundary Fence at Mai Po, Lok Ma Cha and Sha Tau Kok Environmental Permit No. EP-347/2009/A	Title:
			Project Organisation Chart for Phase 2



## Appendix C. Environmental Quality Performance Limits

Table C.1: Action and Limit Levels for Construction Noise

Time Period	Action Level	Limit Level
Daytime (07:00-19:00) except general holidays and Sundays <i>Measurements in <math>L_{eq}</math> (30min)</i>	When one documented complaint is received	75 dB(A)

## Appendix D. Event and Action Plans

Table D.1: Event and Action Plan for Construction Noise

EVENT	ACTION			
	ET Leader	IEC	ER	Contractor
<b>Action Level</b>	<ol style="list-style-type: none"> <li>1. Notify IEC and the Contractor.</li> <li>2. Carry out investigation.</li> <li>3. Report the results of investigation to IEC and the Contractor.</li> <li>4. Discuss with the Contractor and formulate remedial measures.</li> <li>5. Increase monitoring frequency to check mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Review with analyzed results submitted by ET.</li> <li>2. Review the proposed remedial measures by the Contractor and advise ER accordingly.</li> <li>3. Supervise the implement of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing.</li> <li>2. Notify the Contractor.</li> <li>3. Require the Contractor to propose remedial measures for the analyzed noise problem.</li> <li>4. Ensure remedial measures are properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to IEC.</li> <li>2. Implement noise mitigation proposals.</li> </ol>
<b>Limit Level</b>	<ol style="list-style-type: none"> <li>1. Identify the source.</li> <li>2. Notify IEC, ER, EPD and the Contractor.</li> <li>3. Repeat measurement to confirm findings.</li> <li>4. Increase monitoring frequency.</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>6. Inform IEC, ER, and EPD the causes &amp; actions taken for the exceedances.</li> <li>7. Assess effectiveness of the Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET Leader and the Contractor on the potential remedial actions.</li> <li>2. Review the Contractor's remedial actions whenever necessary to assure their effectiveness and advise ER accordingly.</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of exceedance in writing.</li> <li>2. Notify the Contractor.</li> <li>3. Require the Contractor to propose remedial measures for the analyzed noise problem.</li> <li>4. Ensure remedial measures are properly implemented.</li> <li>5. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance.</li> <li>2. Submit proposals for remedial actions to IEC within 3 working days of notification.</li> <li>3. Implement the agreed proposals.</li> <li>4. Resubmit proposals if problem still not under control.</li> <li>5. Stop the relevant activity of works as determined by the ER until the exceedance is abated.</li> </ol>

## Appendix E. Schedule of Mitigation Measures from the EIA Report and EM&A Manual

Table E.1: Recommended Mitigation Measures – Air Quality

EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
2.5.2	3.2.2	<p>The following good site practice should be implemented:</p> <ul style="list-style-type: none"> <li>■ any excavated dusty materials or stockpile of dusty materials should be covered entirely by impervious sheeting or sprayed with water so as to maintain the entire surface wet, and recovered or backfilled or reinstated within 24 hours of the excavation or unloading;</li> <li>■ the working area of excavation should be sprayed with water immediately before, during and immediately after the operations so as to maintain the entire surface wet;</li> <li>■ dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting;</li> <li>■ the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should paved with concrete, bituminous materials or hardcores;</li> <li>■ the portion of road leading only to a construction site that is within 30m of designated vehicle entrance or exit should be kept clear of dusty materials;</li> <li>■ all dusty materials should be sprayed with water prior to any loading, unloading or transfer;</li> <li>■ vehicle speed should be limited to 10kph except on completed access roads;</li> <li>■ every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites.</li> </ul>	Contractor	C	✓

Legend: (1) C - During Construction  
 (2) ✓ - Implemented  
 P - Partially Implemented  
 X - Not Implemented  
 REC - Rectified by Contractor  
 (REC) - Partially Rectified by Contractor  
 ! - Pending Contractor's Rectification Action  
 N/A - Not Applicable

Table E.2: Recommended Mitigation Measures – Noise

EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
3.8.14	4.8.1	<p>The following good site practical should be implemented:</p> <ul style="list-style-type: none"> <li>■ The Contractor shall adopt the Code of Practice on Good Management Practice to Prevent Violation of the Noise Control Ordinance (Chapter 400) (for Construction Industry) published by EPD;</li> <li>■ The Contractor shall observe and comply with the statutory and non-statutory requirements and guidelines;</li> <li>■ Before commencing any work, the Contractor shall submit to the Engineer Representative for approval the method of working, equipment and noise mitigation measures intended to be used at the site;</li> <li>■ The Contractor shall devise and execute working methods to minimise the noise impact on the surrounding sensitive uses, and provide experienced personnel with suitable training to ensure that those methods are implemented;</li> <li>■ Noisy equipment and noisy activities should be located as far away from the Noise Sensitive Receivers (NSRs) as is practical;</li> <li>■ Unused equipment should be turned off. Powered Mechanical Equipment (PME) should be kept to a minimum and the parallel use of noisy equipment / machinery should be avoided;</li> <li>■ Regular maintenance of all plant and equipment;</li> <li>■ Material stockpiles and other structures should be effectively utilised as noise barriers, where practicable.</li> </ul>	Contractor	C	✓
3.8.1 - 3.8.3	4.8.2 - 4.8.3	<p>Other than good site practice, the Contractor is required to adopt Levels 1 and 2 site-specific direct mitigation measures as specified below during the construction phase.</p> <p>With construction / demolition work undertaken at a distance of 60m or less to the NSRs, below mitigation measures should be included:</p> <p><b>Level 1 – Use of Quiet Plant and Movable Noise Barrier</b></p> <ul style="list-style-type: none"> <li>■ The Contractor shall obtain particular models of plant that are quieter than standards given in the Technical Memorandum on Noise from Construction Work other than Percussive Piling (GW-TM).</li> <li>■ Purpose-built movable noise barriers should be used to mitigate construction noise directly at sources that are not usually mobile provide that the direct line of sight to the source is blocked.</li> </ul>	Contractor	C	N/A
3.8.9	4.8.4	<p>In addition to the use of quiet plant and movable noise barrier, alternative demolition method of existing boundary fence at Section 2-3 shall be used where demolition works would be undertaken at a distance of 12m or less to the NSRs. These particular mitigation measures should be included:</p> <p><b>Level 2 – Alternative Demolition Method of Existing Boundary Fence</b></p> <ul style="list-style-type: none"> <li>■ The use of welder is recommended to replace the use of hand-held driller;</li> <li>■ The use of hand-held breaker with movable noise barrier is recommended to replace the use of mini-robot mounted breaker; and the duration for the use of hand-held breaker is minimal as only the surface level of the footing to be broken; and</li> <li>■ The removal of the footing of the existing boundary fence should be carried by concrete crusher mini-robot mounted after the surface level broken by hand-held breaker.</li> </ul>	Contractor	C	N/A
<p>Legend: (1) C - During Construction</p> <p>(2) ✓ - Implemented (REC) - Partially Rectified by Contractor</p> <p>P - Partially Implemented ! - Pending Contractor's Rectification Action</p> <p>X - Not Implemented N/A - Not Applicable</p> <p>REC - Rectified by Contractor</p>					

Table E.3: Recommended Mitigation Measures – Water Quality

EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
4.7.1	5.3.1	<p>Good site practices in addition to the implementation of mitigation measures would minimize the impact to the surrounding environment.</p> <p><i>General Prevention and Precaution Measures:</i></p> <ul style="list-style-type: none"> <li>■ The site should be confined to avoid silt runoff to the site.</li> <li>■ No discharge of silty water into the storm drain and drainage channel within and the vicinity of the site.</li> <li>■ Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials.</li> <li>■ Stockpiles to be covered by tarpaulin to avoid spreading of materials during rainstorms;</li> <li>■ Suitable containers shall be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport;</li> <li>■ Chemical waste containers shall be labelled with appropriate warning signs in English and Chinese to avoid accidents. there shall also be clear instructions showing what action to take in the event of an accidental;</li> <li>■ Storage areas shall be selected at safe locations on site and adequate space shall be allocated to the storage area;</li> <li>■ Any construction plant which causes pollution to the water system due to leakage of oil or fuel shall be removed off-site immediately;</li> <li>■ Spillage or leakage of chemical waste to be controlled by using suitable absorbent materials;</li> <li>■ Chemicals will always be stored on drip trays or in bunded areas where the volume is 110% of the stored volume;</li> <li>■ Regular clearance of domestic waste generated in the temporary sanitary facilities to avoid waste water spillage.</li> <li>■ Temporary sanitary facilities to be provided for on-site workers during construction.</li> </ul>	Contractor	C	✓
4.7.2 - 4.7.3	5.3.2 - 5.3.3	<p><b>Concreting Work</b></p> <p>A temporary drainage channel and associated facilities should be provided to collect the runoff generated and prevent concrete-contaminated water from entering watercourses. Adjustment of pH can be achieved by adding a suitable neutralising reagent to wastewater prior to discharge.</p> <p>The concreting works should be temporarily isolated with proper methods, such as by placing of sandbags or silt curtains with lead edge at bottom and properly supported props.</p>	Contractor	C	N/A
4.7.4	5.3.4	<p><b>Soil Excavation and Stockpiling</b></p> <p>Excavated soil which needs to be temporarily stockpiled should be stored in a specially designated area and provided with a tarpaulin cover to avoid runoff into the drainage channels.</p>	Contractor	C	N/A

Construction of a Secondary Boundary Fence and New Sections of Primary Boundary Fence and Boundary Patrol Road  
Improvement Works for Mai Po, Lok Ma Chau, Sha Tau Kok and Planting Works at Tak Yuet Lau – Monthly EM&A Report for September 2015



EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
4.7.5 - 4.7.6	5.3.5 - 5.3.6	<p><b>Site Depot</b></p> <p>All compounds in works areas should be located on areas of hard standing with provision of drainage channels and settlement ponds where necessary to allow interception and controlled release of settled/treated water. Hard standing compounds should drain via an oil interceptor. The oil interceptor should be regularly inspected and cleaned to avoid wash-out of oil during storm conditions. A bypass should be provided to avoid overload of the interceptor's capacity. Any contractor generating waste oil or other chemicals as a result of his activities should register as a chemical waste producer. Disposal of the waste oil should be done by a licensed collector.</p> <p>Good housekeeping practices should be implemented to minimise careless spillage and to keep the storage and the work space in a tidy and clean condition. Appropriate training including safety codes and relevant manuals should be given to the personnel who regularly handle the chemicals on site.</p>	Contractor	C	✓
4.7.7	5.3.7	<p><b>Construction of Checkpoint</b></p> <p>Sewage system should be constructed to divert domestic sewage, which will be generated from the sanitary facilities provided in the new checkpoint at Sha Tau Kok, to public sewer connected to government sewage treatment facilities.</p>	Contractor	C	✓

- Legend: (1) C - During Construction
- (2) ✓ - Implemented  
P - Partially Implemented  
X - Not Implemented  
REC - Rectified by Contractor  
(REC) - Partially Rectified by Contractor  
! - Pending Contractor's Rectification Action  
N/A - Not Applicable

Table E.4: Recommended Mitigation Measures – Waste Management

EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
5.6.7	6.3.6	<p><b>Site Clearance</b></p> <p>The topsoil and vegetation removed and excavated material may have to be temporarily stockpiled on-site. Control measures should be taken at the stockpiling area to prevent the generation of dust and pollution of stormwater channels, fish ponds or river channels. However, to eliminate the risk of blocking drains in the wet season, it is recommended that stockpiling of excavated materials during the wet season should be avoided as far as practicable.</p>	Contractor	C	N/A
5.6.10 - 5.6.12	6.3.8	<p><b>Construction and Demolition Materials</b></p> <p>Careful design, planning and good site management can minimize over-ordering and generation of waste materials such as concrete mortars and cement grouts. The design of formwork should maximize the use of standard wooden panels so to achieve high reuse levels. Alternatives such as steel formwork or plastic facing should be considered to increase the potential for reuse.</p> <p>The Contractor should recycle as much of the C&amp;D materials as possible on-site. Proper segregation of waste on-site will increase the feasibility of certain components of the waste stream by the recycling contractors. Different areas of the worksite shall be designated for such segregation and storage wherever site conditions permit.</p> <p>Trip-ticket system should be employed to monitor the disposal of C&amp;D material and solid at public filling facilities and landfills, and to control fly-tipping. Government has established a differentiated charging scheme for the disposal of waste to landfill, construction waste sorting facilities and public fill facilities. This will provide additional incentives to reduce the volume of waste generated and to ensure proper segregation of wastes.</p>	Contractor	C	✓
5.6.13 - 5.6.14	6.3.9 - 6.3.13	<p><b>Chemical Waste</b></p> <p>For those processes which generate chemical waste, it may be possible to find alternatives which generate reduced quantities or even no chemical waste, or less dangerous types of chemical waste. Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be handed in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Waste as follows:</p> <p>Containers used for the storage of chemical wastes should:</p> <ul style="list-style-type: none"> <li>■ be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed;</li> <li>■ have a capacity of less than 450 litres unless the specification have been approved by the EPD; and</li> <li>■ display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations,</li> </ul> <p>The storage area for chemical wastes should:</p> <ul style="list-style-type: none"> <li>■ be clearly labelled and used solely for the storage of chemical waste;</li> <li>■ be enclosed on at least 3 sides;</li> <li>■ have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area</li> </ul>	Contractor	PL	N/A

Construction of a Secondary Boundary Fence and New Sections of Primary Boundary Fence and Boundary Patrol Road  
Improvement Works for Mai Po, Lok Ma Chau, Sha Tau Kok and Planting Works at Tak Yuet Lau – Monthly EM&A Report for September 2015



EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
		<p>whichever is the greatest;</p> <ul style="list-style-type: none"> <li>■ have adequate ventilation;</li> <li>■ be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste if necessary); and</li> <li>■ be arranged so that incompatible materials are adequately separated.</li> </ul> <p>Disposal of chemical waste should:</p> <ul style="list-style-type: none"> <li>■ be via a licensed waste collector; and</li> <li>■ be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Facility which also offers a chemical waste collection service and can supply the necessary storage containers, or</li> <li>■ to be re-user of the waste, under approval from the EPD.</li> </ul>			
5.6.16	6.3.15	<p><b>General Refuse</b></p> <p>Should be stored in enclosed bins or compaction units separate from C&amp;D and chemical wastes. The Contractor should employ a reputable waste collector to remove general refuse from the site, separate from C&amp;D and chemical wastes, on a regular basis to minimise odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law.</p>	Contractor	C	✓
5.6.18	6.3.16	<p><b>Construction Waste Management Plan</b></p> <p>A construction waste management plan (CWMP) should be prepared and developed by the contractor to ensure proper collection, treatment and disposal of waste on site. This CWMP will also take into account the requirement to handle chemical wastes on site which will need to be managed by a licensed waste collection contractor.</p>	Contractor	C	✓

- Legend: (1) C - During Construction  
 PL - During Construction Planning
- (2) ✓ - Implemented  
 P - Partially Implemented  
 X - Not Implemented  
 REC - Rectified by Contractor  
 (REC) - Partially Rectified by Contractor  
 ! - Pending Contractor's Rectification Action  
 N/A - Not Applicable



Table E.5: Recommended Mitigation Measures – Ecology

EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
Table 6.38	7.2	<b>Ecological Impacts on Floral Species of Conservation Concern</b> <ul style="list-style-type: none"> <li>Erection of protective fencing to protect the plant during construction period</li> </ul>	Contractor	C	✓
Table 6.40	7.2	<b>Potential Ecological Impacts on Offsite Habitats</b> <ul style="list-style-type: none"> <li>Good site practices for controlling the dust and water quality (avoid stockpiles adjacent to wetlands, covering the stockpiles with impervious sheeting, control of vehicle speed, no discharge of silty water to the rivers, streams and drainage channels);</li> <li>Clear definition of works limit to avoid impact on adjacent habitats.</li> </ul>	Contractor	C	✓
Table 6.39 - Table 6.45	7.2	<b>Disturbance to Wetland-Dependent Birds, Raptors, Terrestrial Birds and Egretty</b> <ul style="list-style-type: none"> <li>Good working practices include switching off unused equipment, keep minimum number of powered mechanical equipment in operation at the same period, the use of stockpiles and other structures to form noise barriers where practicable, avoidance of feeding the wildlife to cause disturbance, site confinement and proper cover of stockpiles with impervious sheeting to minimize construction noise, uncontrolled surface runoff and discharge of silts;</li> <li>Avoidance of construction works using Power Mechanical Equipments within the Wetland Conservation Area during bird migratory season (15th November – 15th March); and</li> <li>Restriction of excavation works within a 150m buffer zone from the egretty to ardeid non-breeding season (from August to February).</li> </ul>	Contractor	C	✓

- Legend: (1) C - During Construction  
(2) ✓ - Implemented  
P - Partially Implemented  
X - Not Implemented  
REC - Rectified by Contractor  
(REC) - Partially Rectified by Contractor  
! - Pending Contractor's Rectification Action  
N/A - Not Applicable

Table E.6: Recommended Mitigation Measures – Landscape and Visual

EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
<b>Preservation of Existing Vegetation</b>					
Table 7-13 CP1	Table 9-1	<ul style="list-style-type: none"> <li>To retain trees that have high amenity or ecology value and contribute most to the landscape and visual amenity of the site and its immediate environs.</li> </ul>	Project Landscape Architect / Contractor	C1	✓
Table 7-13 CP1	Table 9-1	<ul style="list-style-type: none"> <li>Creation of precautionary area around trees to be retained equal to half of the trees canopy diameter. Precautionary area to be fenced.</li> </ul>	Project Landscape Architect / Contractor	BC	✓
Table 7-13 CP1	Table 9-1	<ul style="list-style-type: none"> <li>Prohibition of the storage of materials including fuel, the movement of construction vehicles, and the refuelling and washing of equipment including concrete mixers within the precautionary area.</li> </ul>	Project Landscape Architect / Contractor	C1	✓
Table 7-13 CP1	Table 9-1	<ul style="list-style-type: none"> <li>Phased segmental root pruning for trees to be retained and transplanted over a suitable period (determined by species and size) prior to lifting or site formation works which affect the existing rootball of trees identified for retention. The extent of the pruning will be based on the size and the species of the tree in each case.</li> </ul>	Project Landscape Architect / Contractor	C1	✓
Table 7-13 CP1	Table 9-1	<ul style="list-style-type: none"> <li>Pruning of the branches of existing trees identified for transplantation and retention to be based on the principle of crown thinning maintaining their form and amenity value.</li> </ul>	Project Landscape Architect / Contractor	C1	✓
Table 7-13 CP1	Table 9-1	<ul style="list-style-type: none"> <li>The watering of existing vegetation particularly during periods of excavation when the water table beneath the existing vegetation is lowered.</li> </ul>	Project Landscape Architect / Contractor	C1	N/A
Table 7-13 CP1	Table 9-1	<ul style="list-style-type: none"> <li>The rectification and repair of damaged vegetation following the construction phase to its original condition prior to the commencement of the works or replacement using specimens of the same species, size and form where appropriate to the design intention of the area affected.</li> </ul>	Project Landscape Architect / Contractor	C1	✓
Table 7-13 CP1	Table 9-1	<ul style="list-style-type: none"> <li>All works affecting the trees identified for retention and transplantation will be carefully monitored. This includes the key stages in the preparation of the trees, the implementation of protection measures and health monitoring through out the construction period.</li> </ul>	Project Landscape Architect / Contractor	C1	✓
Table 7-13 CP1	Table 9-1	<ul style="list-style-type: none"> <li>Detailed landscape and tree preservation proposals will be submitted to the relevant government departments for approval under the lease conditions and in accordance with ETWB TCW No. 2/2004 and WBTC No. 3/2006.</li> </ul>	Project Landscape Architect / Contractor	C1	✓
Table 7-13 CP1	Table 9-1	<ul style="list-style-type: none"> <li>The tree preservation works should be implemented by approved Landscape Contractors and inspected and approved on site by a qualified Landscape Architect. A tree protection specification would be included within the contract documents.</li> </ul>	Contractor	C1	✓
<b>Preservation of Existing Topsoil</b>					
Table 7-13 CP2	Table 9-1	<ul style="list-style-type: none"> <li>Topsoil disturbed during the construction phase should be tested using a standard soil testing methodology and where it is found to be worthy of retention stored for re-use.</li> </ul>	Contractor	C1	✓

Construction of a Secondary Boundary Fence and New Sections of Primary Boundary Fence and Boundary Patrol Road Improvement Works for Mai Po, Lok Ma Chau, Sha Tau Kok and Planting Works at Tak Yuet Lau – Monthly EM&A Report for September 2015



EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
Table 7-13 CP2	Table 9-1	<ul style="list-style-type: none"> <li>The soil will be stockpiled to a maximum height of 2m and will be either temporarily vegetated with hydroseeded grass during construction or covered with a waterproof covering to prevent erosion.</li> </ul>	Contractor	C1	✓
Table 7-13 CP2	Table 9-1	<ul style="list-style-type: none"> <li>The stockpile should be turned over on a regular basis to avoid acidification and the degradation of the organic material, and reused after completion. Alternatively, if this is not practicable, it should be considered for use elsewhere, including other projects.</li> </ul>	Contractor	C1	✓
<b>Permanent and Temporary Works Areas</b>					
Table 7-13 CP3	Table 9-1	<ul style="list-style-type: none"> <li>Where appropriate to the final design the landscape of these works areas should be restored following the completion of the construction phase.</li> </ul>	Contractor	C1	✓
Table 7-13 CP3	Table 9-1	<ul style="list-style-type: none"> <li>Construction site controls should be enforced including the storage of materials, the location and appearance of site accommodation and the careful design of site lighting to prevent light spillage.</li> </ul>	Contractor	C1	✓
<b>Mitigation Planting</b>					
Table 7-13 CP4	Table 9-1	<ul style="list-style-type: none"> <li>Replanting of disturbed vegetation should be undertaken at the earliest possible stage of the construction phase.</li> </ul>	Contractor	C1	✓
Table 7-13 CP4	Table 9-1	<ul style="list-style-type: none"> <li>Use of native plant species predominantly in the planting design for the buffer areas.</li> </ul>	Contractor	C1	✓
Table 7-13 CP4	Table 9-1	<ul style="list-style-type: none"> <li>The tree planting works should be implemented by approved Landscape Contractors and inspected and approved on site by a qualified Landscape Architect. A tree planting specification would be included within the contract documents.</li> </ul>	Contractor	C1	✓
<b>Transplantation of Existing Trees</b>					
Table 7-13 CP5	Table 9-1	<ul style="list-style-type: none"> <li>The tree transplanting works should be implemented by approved Landscape Contractors and inspected and approved on site by a qualified Landscape Architect. A tree protection / transplanting specification would be included within the contract documents.</li> </ul>	Contractor	BC1	✓
<b>Design of the Fence and associated Structures</b>					
Table 7-14 OP1	Table 9-2	<p>Design of Boundary Fence, Boundary Patrol Road and Police Check Point – These structural elements will be designed in accordance with security requirement from Police Force and incorporate design features as part of design mitigation measures including:</p> <ol style="list-style-type: none"> <li>Integrated design approach – the boundary fence should be integrated, as far as technically feasible, with existing built structures such as existing road, footpath and track and embankment of fishponds, river and drainage channel as part of design mitigation measures to reduce the potential cumulative impact of the proposed works. The location and orientation of the police check points should be away from landscape and visually sensitive areas such as wetland, fishpond and agricultural field.</li> <li>Building massing - the proposed use of simple</li> </ol>	ArchSD	D	✓

216727/ENL/12/09/A October 2015

P:\Hong Kong\INF\Projects\216727-Boundary Fence\Environmental\Environmental Team\Phase 2\Deliverable\Monthly EM&A Report\2015-09\EM&A Report (Sep 2015) Rev A-draft.doc

EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
		<p>responsive design for the built structures with a low building height profile to reduce the potential visual mass of the structure within a rural context.</p> <p>3. Treatment of built structures - the architectural design should seek to reduce the apparent visual mass of the facilities further through the use of natural materials such as wooden frame, vertical greening or other sustainable materials such as recycled plastic.</p> <p>4. Responsive building and fence finishes - In terms of the proposed finishes natural tones should be considered for the colour palette with non-reflective finishes are recommended to reduce glare effect. The use of colour blocking on the proposed fence could be used to break up the visual mass of the structure.</p> <p>5. Responsive lighting design – Aesthetic design of architectural and track lighting with following glare design measures:</p> <ul style="list-style-type: none"> <li>– Directional and full cut off lighting is recommended particularly for areas adjacent to existing village to minimise light spillage.</li> <li>– Minimise geographical spread of lighting, only applied for safety and security reasons;</li> <li>– Limited lighting intensity to meet the minimum safety and operation requirement; and</li> <li>– High-pressure sodium road lighting is recommended for more stringent light control reducing spillage and thus visual impacts.</li> </ul>			
<b>Compensatory Planting Proposals</b>					
Table 7-14 OP2	Table 9-2	<ul style="list-style-type: none"> <li>■ Utilise native to Hong Kong will be utilized within the buffer planting areas.</li> </ul>	Contractor	D	✓
Table 7-14 OP2/3	Table 9-2	<ul style="list-style-type: none"> <li>■ A qualified or registered landscape architect will be involved in the design, construction supervision and monitoring, and maintenance period to oversee the implementation of the recommended landscape and visual mitigation measures including the tree preservation and landscape works on site.</li> </ul>	Contractor	D	✓
Table 7-14 OP2	Table 9-2	<p>Tree and Shrub Planting – Given the rural nature of the proposed alignment it is recommended that the where possible tree and shrub species which are native to Hong Kong be used. In addition where possible the planting of new trees and shrubs will aim to link together existing woodland areas and small tree groups to improve the connectivity between habitats and create more coherent landscape framework. The planting of small groups of trees along the alignment of the proposed fence will serve to de-emphasise the horizontality of the fence structure and provide for better sense of visual integration with the landscape context. Where practicable vertical greening measures should also be considered on engineering structures.</p>	Contractor	D	✓
Table 7-14 OP2	Table 9-2	<p>Compensatory Planting Proposals – Given the works extent is largely limited along existing roadside embankment to minimise impact to existing village settlements and valuable landscape resources such as wetland, fishpond, stream course and existing trees, and considered the importance of</p>	Contractor	D	✓

Construction of a Secondary Boundary Fence and New Sections of Primary Boundary Fence and Boundary Patrol Road Improvement Works for Mai Po, Lok Ma Chau, Sha Tau Kok and Planting Works at Tak Yuet Lau – Monthly EM&A Report for September 2015



EIA Ref.	EM&A Manual Ref.	Recommended Mitigation Measures	Who to implement?	When to implement? (1)	Implementation Status (2)
		<p>tree retention within the works area, new tree planting will concentrate in selected new amenity areas along the alignment, infilling between retained and transplanted trees. The preliminary planting proposals for the proposed works include the planting of some 357 new trees utilising a combination of mature to light standard sized stock (i.e. approximately 15% of mature trees, 75% of standard trees, and 10% light standard trees). These trees will be planted in woodland clumps and small tree groups at strategic locations to de-emphasise the horizontality of the fence alignment. Based on preliminary findings the proposed planting will result in a compensatory planting ratio of 1:1 (new planting: trees recommended for felling). This compares favourably with the report's assertion that some 357 trees would be felled due to the proposed works. With the proposed preservation of existing trees, transplantation of trees in conflict with the proposals and the planting of new trees the project area will contain approximately 2000 trees. Trees forming part of the new planting will provide screening to neighbourhood villagers and will utilise species native to Hong Kong. These proposals will be subject to review at detailed design stage of the project.</p>			

- Legend: (1) C1 - Throughout Construction Phase  
 BC - Before Construction Phase Commences  
 BC1 - Prior to the Commencement of the Proposed Works  
 D - Throughout Design Phase
- (2) ✓ - Implemented  
 P - Partially Implemented  
 X - Not Implemented  
 REC - Rectified by Contractor  
 (REC) - Partially Rectified by Contractor  
 ! - Pending Contractor's Rectification Action  
 N/A - Not Applicable

# Appendix F. EM&A Schedule

Environmental Monitoring and Audit Schedule for September 2015

Sun	Mon	Tue	Wed	Thu	Fri	Sat
		1	2	3	4	5
				The 70th anniversary day of the victory of the Chinese people's war of resistance against Japanese aggression	*	
6	7	8	9	10	11	12
			*			
13	14	15	16	17	18	19
					*	
20	21	22	23	24	25	26
			**			
27	28	29	30			
	The day following the Chinese Mid-Autumn Festival		*			

- Noise Monitoring
- \* Site Audit by Environmental Team (ET)
- \*\* Site Audit with Independent Environmental Checker (IEC)
- @ Report Submission (EM&A Report)
- Public Holiday

Construction of a Secondary Boundary Fence and New Sections of Primary Boundary Fence and Boundary Patrol Road  
 Improvement Works for Mai Po, Lok Ma Chau, Sha Tau Kok and Planting Works at Tak Yuet Lau – Monthly EM&A Report for September 2015



Tentative Environmental Monitoring and Audit Schedule for October 2015

Sun	Mon	Tue	Wed	Thu	Fri	Sat
				1 National Day	2 *	3
4	5	6	7 *	8	9	10
11	12	13	14 @ *	15	16	17
18	19	20	21 Chung Yeung Festival	22	23 **	24
25	26	27	28 *	29	30	31

- Noise Monitoring
- \* Site Audit by Environmental Team (ET)
- \*\* Site Audit with Independent Environmental Checker (IEC)
- @ Report Submission (EM&A Report)
- Public Holiday

## Appendix G. Calibration Certificates





# Calibration Certificate

Certificate No. **503993**

Page 1 of 2 Pages

**Customer :** Mott MacDonald Hong Kong Limited

**Address :** 20/F, Two Landmark East, 100 How Ming Street, Kwun Tong, Kowloon, Hong Kong.

**Order No. :** Q51536

**Date of receipt :** 15-May-15

## Item Tested

**Description :** Acoustic Calibrator

**Manufacturer :** Castle

**Model :** GA607

**Serial No. :** 040162

## Test Conditions

**Date of Test :** 3-Jun-15

**Supply Voltage :** --

**Ambient Temperature :** (23 ± 3)°C

**Relative Humidity :** (50 ± 25) %

## Test Specifications

Calibration check.

Ref. Document/Procedure : F06, F20, Z02.

## Test Results

All results were within the IEC 942 Class 1 specification.

The results are shown in the attached page(s).

Main Test equipment used:


<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S014	Spectrum Analyzer	405316	NIM-PRC & SCL-HKSAR
S240	Sound Level Calibrator	500563	NIM-PRC & SCL-HKSAR
S041	Universal Counter	405317	SCL-HKSAR
S206	Sound Level Meter	405322	SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI).

The test results apply to the above Unit-Under-Test only

**Calibrated by :**

  
Dorothy Cheuk

**Approved by :**

  
Steve Kwan

**Date:** 3-Jun-15

This Certificate is issued by:  
Hong Kong Calibration Ltd.  
Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.  
Tel: 2425 8801 Fax: 2425 8646

The copyright of this certificate is owned by Hong Kong Calibration Ltd. It may not be reproduced except in full.



# Calibration Certificate

Certificate No. 503993

Page 2 of 2 Pages

Results :

## 1. Level Accuracy

UUT Setting (dB)	Measured Value (dB)	IEC 942 Class 1 Spec.
94.0	94.1	± 0.3 dB

Uncertainty : ± 0.2 dB

## 2. Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	IEC 942 Class 1 Spec.
1.000	1.0000	± 2 %

Uncertainty : ± 3.6 x 10<sup>-6</sup>

- 3. Level Stability : 0.0 dB**  
IEC 942 Class 1 Spec.: ± 0.1 dB  
Uncertainty : ± 0.01 dB

- 4. Total Harmonic Distortion : < 1.0 %**  
IEC 942 Class 1 Spec. : < 3 %  
Uncertainty : ± 2.3 % of rdg.

- Remark : 1. UUT : Unit-Under-Test  
2. The above measured values were the mean of 3 measurements.  
3. The uncertainty claimed is for a confidence probability of not less than 95%.  
4. Atmospheric Pressure : 998 hPa.

----- END -----



# Calibration Certificate

Certificate No. **503992**

Page 1 of 3 Pages

**Customer :** Mott MacDonald Hong Kong Limited

**Address :** 20/F, Two Landmark East, 100 How Ming Street, Kwun Tong, Kowloon, Hong Kong.

**Order No. :** Q51536

**Date of receipt :** 15-May-15

## Item Tested

**Description :** Precision Integrating Sound Level Meter

**Manufacturer :** Rion

**Model :** NL-31

**Serial No. :** 01262786

## Test Conditions

**Date of Test :** 3-Jun-15

**Supply Voltage :** --

**Ambient Temperature :** (23 ± 3)°C

**Relative Humidity :** (50 ± 25) %

## Test Specifications

Calibration check.

Ref. Document/Procedure : Z01, IEC 651, IEC 804.

## Test Results

All results were within the IEC 651 Type 1 & IEC 804 Type 1 specification.  
The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S017	Multi-Function Generator	C147450	SCL-HKSAR
S240	Sound Level Calibrator	500563	NIM-PRC & SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI).  
The test results apply to the above Unit-Under-Test only

**Calibrated by :**   
Dorothy Cheuk

**Approved by :**   
Steve Kwan

**Date:** 3-Jun-15

This Certificate is issued by:  
Hong Kong Calibration Ltd.  
Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.  
Tel: 2425 8801 Fax: 2425 8646



# Calibration Certificate

Certificate No. **503992**

Page 2 of 3 Pages

Results :

## 1. SPL Accuracy

UUT Setting			Applied Value (dB)	UUT Reading (dB)
Level Range (dB)	Weight	Response		
20 – 100	L <sub>A</sub>	Fast	94.0	94.0
		Slow		93.9
	L <sub>C</sub>	Fast		94.0
	L <sub>p</sub>	Fast		94.1
30 – 120	L <sub>A</sub>	Fast	94.0	93.9
		Slow		93.9
	L <sub>C</sub>	Fast		94.0
	L <sub>p</sub>	Fast		94.0
30 – 120	L <sub>A</sub>	Fast	114.0	114.0
		Slow		113.9
	L <sub>C</sub>	Fast		114.0
	L <sub>p</sub>	Fast		114.0

IEC 651 Type 1 Spec. :  $\pm 0.7$  dB

Uncertainty :  $\pm 0.1$  dB

## 2. Level Stability : 0.0 dB

IEC 651 Type 1 Spec. :  $\pm 0.3$  dB

Uncertainty :  $\pm 0.01$  dB

## 3. Linearity

### 3.1 Level Linearity

UUT Range (dB)	Applied Value (dB)	UUT Reading (dB)	Variation (dB)	IEC 651 Type 1 Spec. (Primary Indicator Range)
130	114.0	114.0	0.0	$\pm 0.7$ dB
130	104.0	104.0	0.0	
120	94.0	94.0 (Ref.)	--	
110	84.0	84.0	0.0	
100	74.0	74.0	0.0	
90	64.0	64.0	0.0	
80	54.0	54.0	0.0	

Uncertainty :  $\pm 0.1$  dB



# Calibration Certificate

Certificate No. **503992**

Page 3 of 3 Pages

### 3.2 Differential level linearity

UUT Range (dB)	Applied Value (dB)	UUT Reading (dB)	Variation (dB)	IEC 651 Type 1 Spec.
120	84.0	83.9	0.0	± 0.4 dB
	94.0	93.9 (Ref.)	- -	
	95.0	94.9	0.0	± 0.2 dB

Uncertainty : ± 0.1 dB

### 4. Frequency Weighting - A weighting

Frequency	Attenuation (dB)	IEC 651 Type 1 Spec.
31.5 Hz	-39.4	- 39.4 dB, ± 1.5 dB
63 Hz	-26.5	- 26.2 dB, ± 1.5 dB
125 Hz	-16.9	- 16.1 dB, ± 1 dB
250 Hz	-8.7	- 8.6 dB, ± 1 dB
500 Hz	-3.3	- 3.2 dB, ± 1 dB
1 kHz	0.0 (Ref.)	0 dB, ± 1 dB
2 kHz	+1.3	+ 1.2 dB, ± 1 dB
4 kHz	+1.1	+ 1.0 dB, ± 1 dB
8 kHz	-1.1	- 1.1 dB, + 1.5 dB ~ - 3 dB
16 kHz	-6.4	- 6.6 dB, + 3 dB ~ - ∞

Uncertainty : ± 0.1 dB

### 5. Time Averaging

Applied Burst duty Factor	Applied Leq Value (dB)	UUT Reading (dB)	IEC 804 Type 1 Spec.
continuous	40.0	40.0	--
1/10	40.0	39.9	± 0.5 dB
1/10 <sup>2</sup>	40.0	40.0	
1/10 <sup>3</sup>	40.0	40.0	± 1.0 dB
1/10 <sup>4</sup>	40.0	39.9	


Uncertainty : ± 0.1 dB

- Remarks:
1. UUT : Unit-Under-Test
  2. The uncertainty claimed is for a confidence probability of not less than 95%.
  3. Atmospheric Pressure : 998 hPa
  4. The UUT's internal calibration was performed before the calibration.

----- END -----

# Appendix H. Noise Monitoring Results and Graphical Presentation

Daytime Noise Monitoring Results at Station VH03											
Date	Weather Conditions	Wind Speed, m/s	Noise Level for 30-min, dB(A)					Major Construction Noise Sources during monitoring	Other Noise Sources during monitoring	Remarks	
			Start Time	End Time	Leq	L10	L90				
18-Sep-15	Cloudy	2.2	10:08	10:38	45	46	42	Nil	Traffic noise, wild life (not Project-related)	Nil	
23-Sep-15	Cloudy	1.9	10:19	10:49	61	62	61	Nil	Traffic noise, wild life, running water (not Project-related)	Nil	
30-Sep-15	Cloudy	2.2	10:34	11:04	51	55	39	Nil	Traffic noise, wild life (not Project-related)	Nil	
					Min.	45					
					Max.	61					

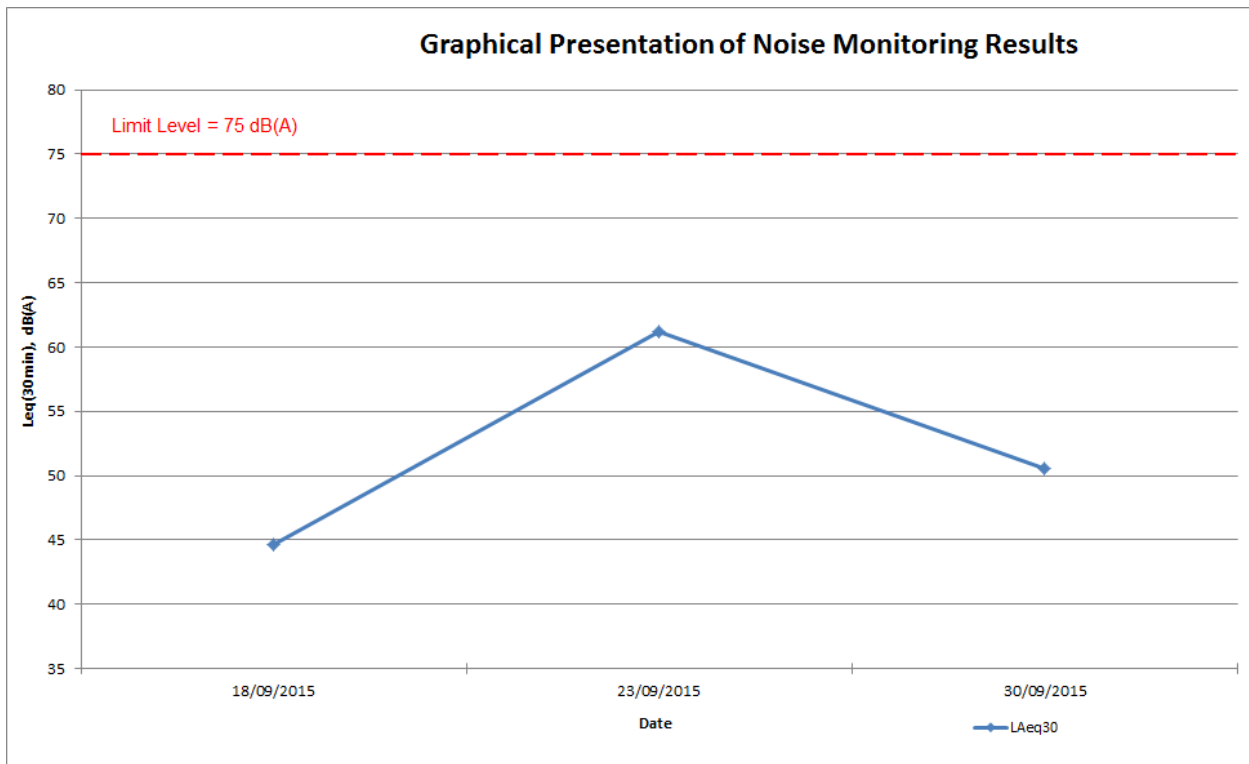

# Appendix I. Monthly Waste Flow Table

Table I.1: Monthly Summary Waste Flow Table for 2015 (from April)

Month	Actual Quantities of Inert C&D Materials Generated Monthly (in '000 m <sup>3</sup> )										Actual Quantities of C&D Wastes Generated Monthly									
	Total Quantity Generated		Broken Concrete		Reused in the Contract		Reused in other Projects		Disposed of at Public Fill		Metals ('000 kg)		Paper/Cardboard ('000 kg)		Plastics ('000 kg)		Chemical waste ('000 kg)		Others (e.g. refuse) ('000 m <sup>3</sup> )	
	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.	Est.	Act.
Jan	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Feb	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Mar	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Apr	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0
May	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0
Jun	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0
<b>Sub-total</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>
Jul	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0
Aug	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0
Sep	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0	-	0
Oct																				
Nov																				
Dec																				
<b>Total</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>	-	<b>0</b>

## Appendix J. Complaint Log

Table J.1: Complaint Log for the Reporting Month

Log Ref.	Location	Complainant / Date of Contact	Details of Complaint	Investigation / Mitigation Action	File Closed
N/A	N/A	N/A	N/A	N/A	N/A

Note: No environmental complaint was received in September 2015.



## Appendix K. Weather Information from Hong Kong Observatory

This Appendix presents wind data obtained from the nearest Hong Kong Observatory monitoring station, at Ta Kwu Ling, during noise impact monitoring days.

**EXTRACT OF METEOROLOGICAL OBSERVATIONS FOR HONG KONG,  
SEPTEMBER 2015 (Table 1)**

Date September	Mean Pressure (hPa)	Air Temperature			Mean Dew Point Temperature (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)
		Maximum (deg. C)	Mean (deg. C)	Minimum (deg. C)				
1	1007.8	28.9	27.4	25.7	25.4	89	87	5.3
2	1010.9	27.7	25.8	24.5	24.8	94	88	39.0
3	1013.0	29.0	27.6	25.8	25.8	90	87	0.2
4	1013.1	32.9	29.1	27.0	25.7	82	60	-
5	1011.1	31.9	29.3	27.2	24.8	78	38	-
6	1008.1	32.3	29.6	27.8	25.6	79	43	-
7	1007.2	29.6	28.3	26.7	25.9	87	82	7.3
8	1009.4	30.7	27.9	26.4	23.1	75	60	-
9	1012.0	31.2	28.2	26.5	23.0	74	44	Trace
10	1012.7	31.3	28.1	26.5	23.2	75	47	-
11	1011.1	31.0	28.1	26.8	23.7	77	46	Trace
12	1011.5	30.5	27.9	26.2	23.2	76	66	Trace
13	1013.0	31.2	28.0	25.8	21.4	68	49	-
14	1012.2	31.4	28.0	25.9	22.1	71	46	-
15	1011.3	31.9	28.6	26.5	23.1	73	60	-
16	1011.9	31.0	28.1	26.9	24.5	81	86	1.5
17	1014.6	30.6	28.2	27.1	24.2	79	72	Trace
18	1015.0	31.8	28.5	26.8	24.0	77	47	Trace
19	1012.2	30.6	28.3	26.8	24.3	79	67	-
20	1009.3	31.1	28.7	27.1	24.5	78	74	Trace
21	1008.6	28.7	27.4	25.5	23.8	81	88	16.9
22	1009.9	31.0	28.1	26.3	25.5	86	67	2.9
23	1009.1	32.0	28.9	27.3	25.3	81	40	Trace
24	1006.7	32.0	29.3	27.4	24.7	77	23	-
25	1004.9	32.2	29.7	28.1	25.3	78	38	-
26	1006.7	32.2	28.7	26.9	26.3	87	71	10.2
27	1008.2	30.2	27.8	26.5	25.0	85	81	4.6
28	1006.7	32.8	29.0	25.8	20.6	61	30	-
29	1005.6	31.3	29.7	27.4	20.0	56	53	-
30	1011.0	32.7	29.8	28.2	24.8	75	78	Trace
Mean/Total	1010.2	31.1	28.4	26.6	24.1	78	61	87.9
Normal*	1008.9	30.1	27.7	25.8	23.4	78	66	327.6
Station	Hong Kong Observatory							

**EXTRACT OF METEOROLOGICAL OBSERVATIONS FOR HONG KONG,  
SEPTEMBER 2015 (Table 2)**

Date September	Number of hours of Reduced Visibility# (hours)	Total Bright Sunshine (hours)	Daily Global Solar Radiation (MJ/m <sup>2</sup> )	Total Evaporation (mm)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
1	0	0.4	9.54	2.6	050	8.6
2	0	-	2.27	1.5	100	16.5
3	0	0.7	10.74	2.4	060	18.2
4	0	8.7	22.09	4.8	080	9.8
5	0	11.0	25.27	6.6	220	11.7
6	0	9.7	23.75	6.0	240	24.9
7	0	0.5	5.72	2.3	250	21.3
8	0	8.3	20.18	6.6	060	29.0
9	0	10.1	23.03	6.5	070	26.2
10	0	7.9	20.86	6.1	060	24.7
11	0	8.4	21.48	6.2	100	21.4
12	0	6.7	18.07	6.3	090	22.6
13	0	9.2	22.46	6.1	050	39.9
14	0	9.3	23.14	7.7	060	41.3
15	0	9.0	23.08	6.1	070	39.5
16	0	2.1	13.90	2.3	070	32.2
17	0	7.1	19.80	5.6	070	27.4
18	0	8.6	20.72	4.3	070	14.5
19	0	3.8	11.39	3.0	180	8.1
20	0	7.7	18.12	6.0	200	14.5
21	0	0.4	7.96	1.6	190	11.9
22	0	8.8	20.78	4.9	110	14.8
23	0	6.8	14.15	3.9	110	10.2
24	0	11.1	23.76	6.2	230	17.3
25	0	11.0	23.62	3.5	230	20.5
26	3	4.7	11.85	3.9	090	14.0
27	0	2.5	9.87	5.6	090	15.1
28	0	11.1	21.98	6.2	010	16.4
29	0	10.4	20.82	5.5	290	15.5
30	0	8.5	19.60	3.6	140	12.7
Mean/Total	3	204.5	17.67	143.9	060	20.0
Normal*	87.5 <sup>§</sup>	172.3	14.61	125.9	090	22.6
Station	Hong Kong International Airport	King's Park		Waglan Island <sup>^</sup>		

The minimum pressure recorded at the Hong Kong Observatory was 1002.7 hectopascals at 1653 HKT on 25 September.

The maximum air temperature recorded at the Hong Kong Observatory was 32.9 degrees C at 1456 HKT on 4 September.

The minimum air temperature recorded at the Hong Kong Observatory was 24.5 degrees C at 1236 HKT on 2 September.

The maximum gust peak speed recorded at Waglan Island was 68 kilometres per hour from 060 degrees at 0159 HKT on 14 September.

The maximum instantaneous rate of rainfall recorded at the Hong Kong Observatory was 157 millimetres per hour at 2349 HKT on 26 September.

# Reduced visibility refers to visibility below 8 kilometres when there is no fog, mist or precipitation.

- The visibility readings at the Hong Kong International Airport are based on hourly observations by professional meteorological observers in 2004 and before, and average readings over the 10-minute period before the clock hour of the visibility meter near the middle of the south runway from 2005 onwards. The change of the data source in 2005 is an improvement of the visibility assessment using instrumented observations following the international trend.

- Before 10 October 2007, the number of hours of reduced visibility at the Hong Kong International Airport in 2005 and thereafter displayed in this web page was based on hourly visibility observations by professional meteorological observers. Since 10 October 2007, the data have been revised using the average visibility readings over the 10-minute period before the clock hour, as recorded by the visibility meter near the middle of the south runway.


^ In case the data are not available from Waglan Island, observations of Cheung Chau or other nearby weather stations will be incorporated in computing the Prevailing Wind Direction and Mean Wind Speed.

\* 1981-2010 Climatological Normal, unless otherwise specified

§ 1997-2014 Mean value




## Wind Data for Ta Kwu Ling

18 Sep 2015

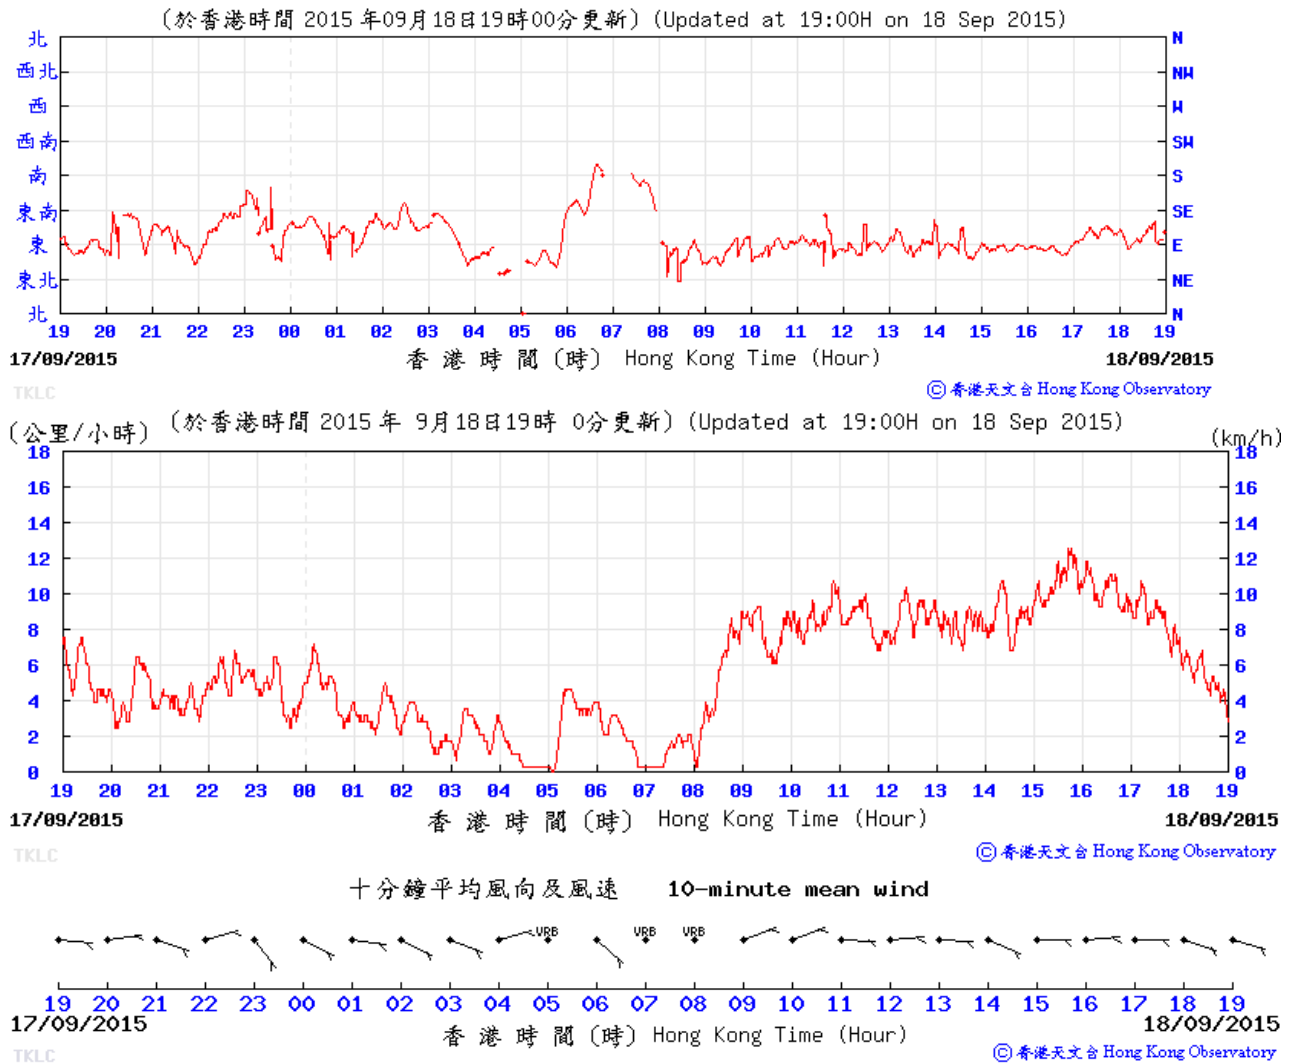




## Wind Data for Ta Kwu Ling

19 Sep 2015

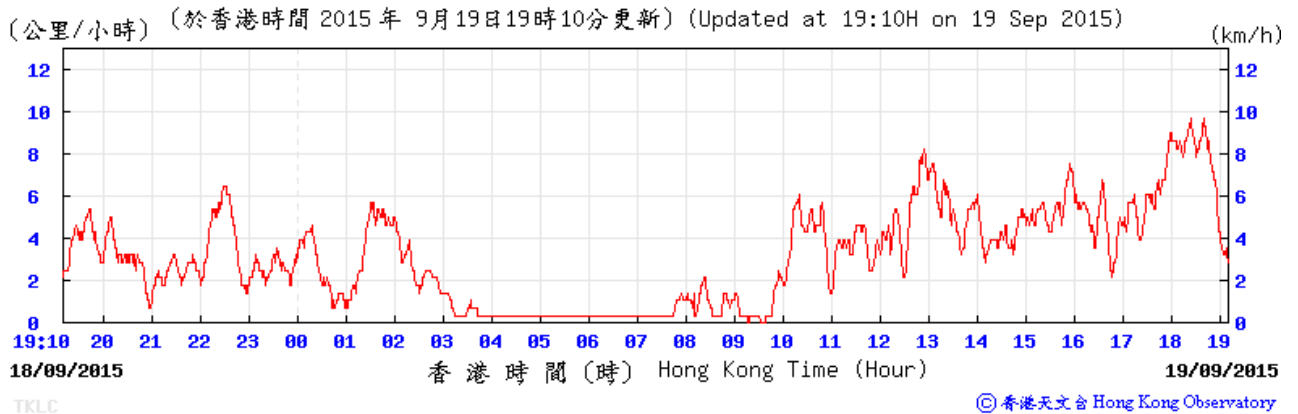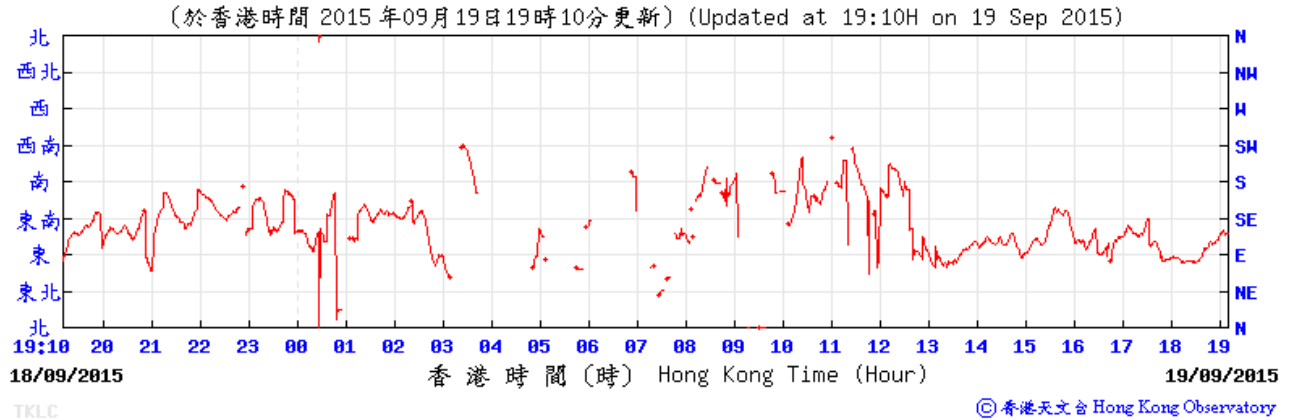




## Wind Data for Ta Kwu Ling

23 Sep 2015

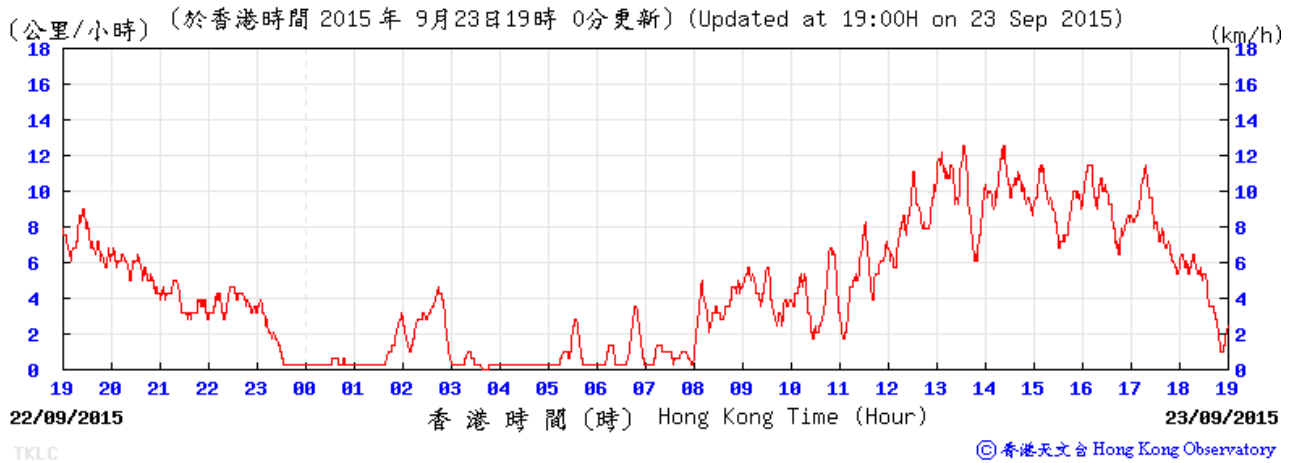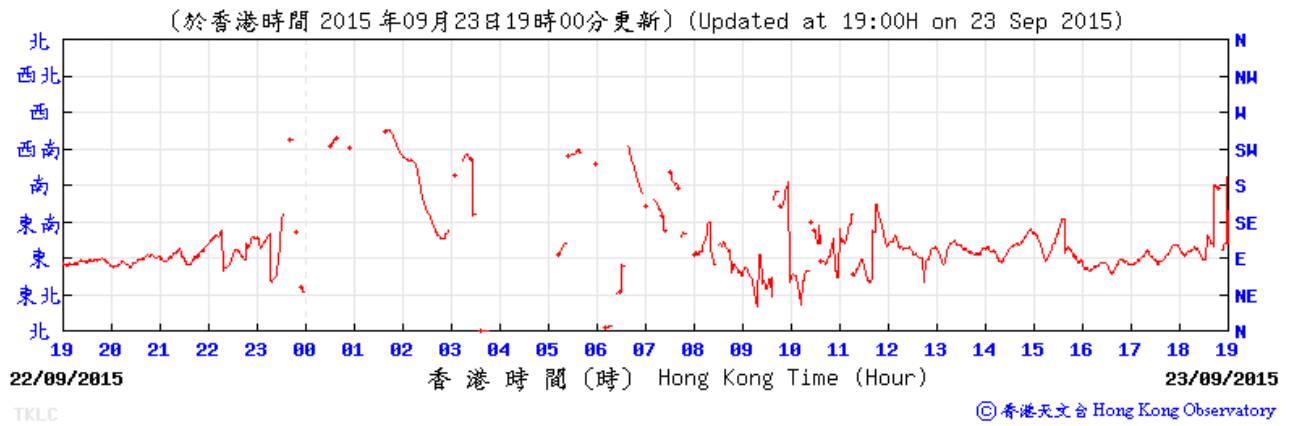

## Wind Data for Ta Kwu Ling


24 Sep 2015

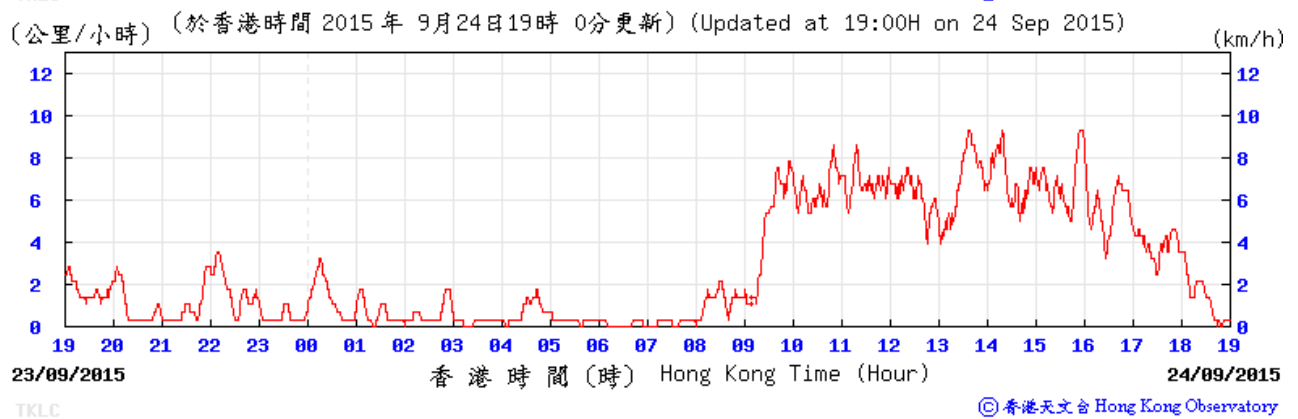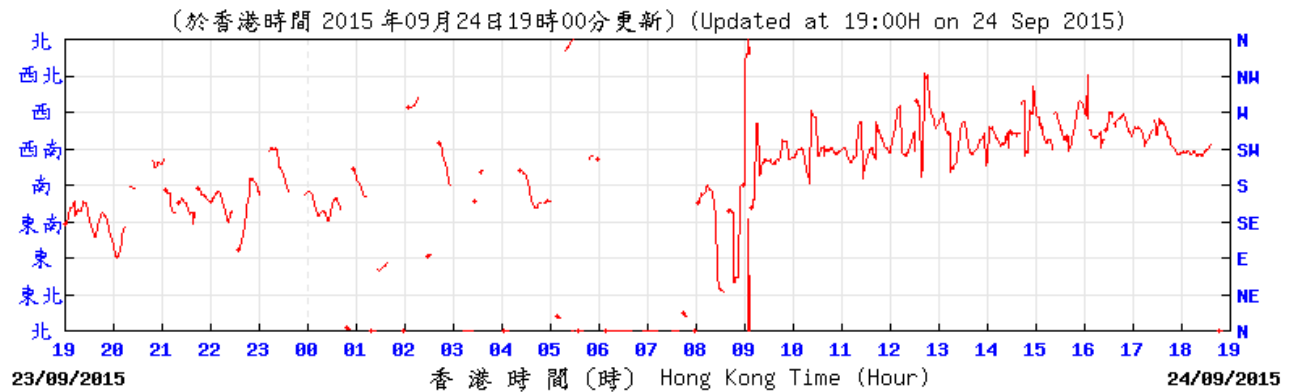



## Wind Data for Ta Kwu Ling

30 Sep 2015

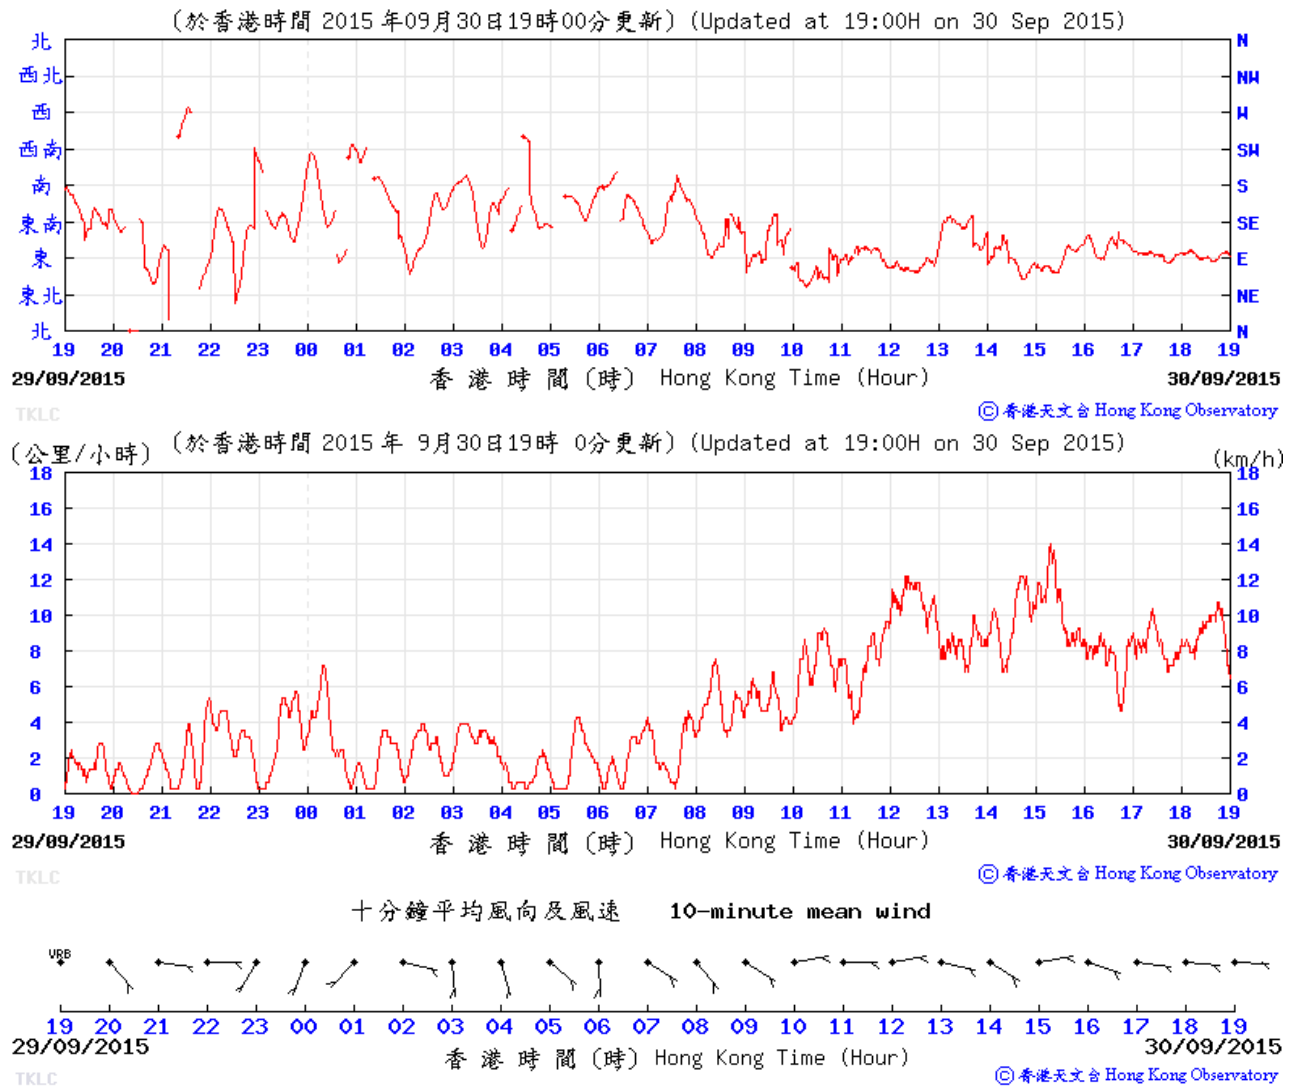

## Wind Data for Ta Kwu Ling

1 Oct 2015

