

Gammon Construction Limited

Contract No. DC/2007/23  
Harbour Area Treatment Scheme  
Stage 2A Construction of Sewage  
Conveyance System from North  
Point to Stonecutters Island: *Thirty-  
fourth Monthly EM&A Report*

October 2012

**Environmental Resources Management**

16/F DCH Commercial Centre  
25 Westlands Road, Quarry Bay  
Hong Kong  
Telephone: (852) 2271 3000  
Facsimile: (852) 2723 5660  
E-mail: [post.hk@erm.com](mailto:post.hk@erm.com)  
<http://www.erm.com>

Gammon Construction Limited

Contract No. DC/2007/23  
Harbour Area Treatment Scheme  
Stage 2A Construction of Sewage  
Conveyance System from North  
Point to Stonecutters Island: *Thirty-  
fourth Monthly EM&A Report*

October 2012

Reference 0104887

For and on behalf of ERM-Hong Kong, Limited	
Approved by:	Frank Wan
Signed:	
Position:	Partner
Certified by:	
	(Environmental Team Leader – Winnie Ko)
Date:	14 October 2012

## CONTENTS

	<b>EXECUTIVE SUMMARY</b>	<i>i</i>
<b>1</b>	<b>INTRODUCTION</b>	<b>1</b>
1.1	<i>PURPOSE OF THE REPORT</i>	1
1.2	<i>STRUCTURE OF THE REPORT</i>	1
<b>2</b>	<b>PROJECT INFORMATION</b>	<b>5</b>
2.1	<i>BACKGROUND AND GENERAL SITE DESCRIPTION</i>	5
2.2	<i>STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS AND REQUIRED SUBMISSIONS</i>	6
2.3	<i>PROJECT ORGANISATION</i>	7
<b>3</b>	<b>NORTH POINT PRODUCTION AND DROP SHAFTS</b>	<b>8</b>
3.1	<i>CONSTRUCTION ACTIVITIES DURING THE REPORTING MONTH</i>	8
3.2	<i>STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS</i>	8
3.3	<i>ENVIRONMENTAL MONITORING REQUIREMENTS</i>	9
3.3.1	<i>Air Quality Monitoring</i>	9
3.3.2	<i>Noise Monitoring</i>	12
3.3.3	<i>Cultural Heritage</i>	14
3.3.4	<i>Landscape and Visual Monitoring</i>	14
3.4	<i>IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS</i>	15
3.5	<i>MONITORING RESULTS</i>	15
3.5.1	<i>Air Quality</i>	15
3.5.2	<i>Noise</i>	15
3.5.3	<i>Landscape and Visual</i>	16
3.5.4	<i>Cultural Heritage</i>	16
3.5.5	<i>Waste Management</i>	16
3.6	<i>ENVIRONMENTAL SITE INSPECTION</i>	17
3.7	<i>ENVIRONMENTAL NON-CONFORMANCE</i>	17
3.7.1	<i>Summary of Monitoring Exceedance</i>	17
3.7.2	<i>Summary of Environmental Non-Compliance</i>	17
3.7.3	<i>Summary of Environmental Complaint</i>	17
3.7.4	<i>Summary of Environmental Summon and Successful Prosecution</i>	17
3.8	<i>FUTURE KEY ISSUES</i>	18
3.8.1	<i>Key Issues for the Coming Months</i>	18
3.8.2	<i>Monitoring Schedule for the Next Month</i>	18
3.8.3	<i>Construction Programme for the Next Month</i>	18
<b>4</b>	<b>WAN CHAI EAST PRODUCTION AND DROP SHAFTS</b>	<b>19</b>
4.1	<i>CONSTRUCTION ACTIVITIES DURING THE REPORTING MONTH</i>	19
4.2	<i>STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS</i>	19
4.3	<i>ENVIRONMENTAL MONITORING REQUIREMENTS</i>	20
4.3.1	<i>Air Quality Monitoring</i>	20

4.3.2	<i>Noise Monitoring</i>	23
4.3.3	<i>Cultural Heritage</i>	25
4.3.4	<i>Landscape and Visual Monitoring</i>	25
4.4	IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS	25
4.5	MONITORING RESULTS	25
4.5.1	<i>Air Quality</i>	25
4.5.2	<i>Noise</i>	26
4.5.3	<i>Landscape and Visual</i>	26
4.5.4	<i>Cultural Heritage</i>	26
4.5.5	<i>Waste Management</i>	26
4.6	ENVIRONMENTAL SITE INSPECTION	27
4.7	ENVIRONMENTAL NON-CONFORMANCE	28
4.7.1	<i>Summary of Monitoring Exceedance</i>	28
4.7.2	<i>Summary of Environmental Non-Compliance</i>	29
4.7.3	<i>Summary of Environmental Complaint</i>	29
4.7.4	<i>Summary of Environmental Summon and Successful Prosecution</i>	29
4.8	FUTURE KEY ISSUES	29
4.8.1	<i>Key Issues for the Coming Month</i>	29
4.8.2	<i>Monitoring Schedule for the Next Month</i>	30
4.8.3	<i>Construction Programme for the Next Month</i>	30
5	CENTRAL DROP SHAFT	31
5.1	CONSTRUCTION ACTIVITIES DURING THE REPORTING MONTH	31
5.2	STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS	31
5.3	ENVIRONMENTAL MONITORING REQUIREMENTS	31
5.3.1	<i>Air Quality Monitoring</i>	31
5.3.2	<i>Noise Monitoring</i>	35
5.3.3	<i>Cultural Heritage</i>	36
5.3.4	<i>Landscape and Visual Monitoring</i>	36
5.4	IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS	37
5.5	MONITORING RESULTS	37
5.5.1	<i>Air Quality</i>	37
5.5.2	<i>Noise</i>	37
5.5.3	<i>Landscape and Visual</i>	37
5.5.4	<i>Cultural Heritage</i>	37
5.5.5	<i>Waste Management</i>	38
5.6	ENVIRONMENTAL SITE INSPECTION	38
5.7	ENVIRONMENTAL NON-CONFORMANCE	39
5.7.1	<i>Summary of Monitoring Exceedance</i>	39
5.7.2	<i>Summary of Environmental Non-Compliance</i>	39
5.7.3	<i>Summary of Environmental Complaint</i>	39
5.7.4	<i>Summary of Environmental Summon and Successful Prosecution</i>	39
5.8	FUTURE KEY ISSUES	39
5.8.1	<i>Key Issues for the Coming Month</i>	39
5.8.2	<i>Monitoring Schedule for the Next Month</i>	39
5.8.3	<i>Construction Programme for the Next Month</i>	39
6	SAI YING PUN JUNCTION SHAFT	40
6.1	CONSTRUCTION ACTIVITIES DURING THE REPORTING MONTH	40
6.2	STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS	40

6.3	ENVIRONMENTAL MONITORING REQUIREMENTS	40
6.3.1	<i>Air Quality Monitoring</i>	40
6.3.2	<i>Noise Monitoring</i>	42
6.3.3	<i>Cultural Heritage</i>	43
6.3.4	<i>Landscape and Visual Monitoring</i>	43
6.4	IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS	44
6.5	MONITORING RESULTS	44
6.5.1	<i>Air Quality</i>	44
6.5.2	<i>Noise</i>	44
6.5.3	<i>Landscape and Visual</i>	44
6.5.4	<i>Cultural Heritage</i>	44
6.5.5	<i>Waste Management</i>	45
6.6	ENVIRONMENTAL SITE INSPECTION	45
6.7	ENVIRONMENTAL NON-CONFORMANCE	46
6.7.1	<i>Summary of Monitoring Exceedance</i>	46
6.7.2	<i>Summary of Environmental Non-Compliance</i>	46
6.7.3	<i>Summary of Environmental Complaint</i>	46
6.7.4	<i>Summary of Environmental Summon and Successful Prosecution</i>	46
6.8	FUTURE KEY ISSUES	46
6.8.1	<i>Key Issues for the Coming Month</i>	46
6.8.2	<i>Monitoring Schedule for the Next Month</i>	46
6.8.3	<i>Construction Programme for the Next Month</i>	46
7	STONECUTTERS ISLAND PRODUCTION AND RISER SHAFTS	47
7.1	CONSTRUCTION ACTIVITIES DURING THE REPORTING MONTH	47
7.2	STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS	47
7.3	ENVIRONMENTAL MONITORING REQUIREMENTS	47
7.3.1	<i>Air Quality Monitoring</i>	47
7.3.2	<i>Noise Monitoring</i>	51
7.3.3	<i>Cultural Heritage</i>	53
7.3.4	<i>Landscape and Visual Monitoring</i>	53
7.4	IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS	54
7.5	MONITORING RESULTS	54
7.5.1	<i>Air Quality</i>	54
7.5.2	<i>Noise</i>	54
7.5.3	<i>Landscape and Visual</i>	55
7.5.4	<i>Cultural Heritage</i>	55
7.5.5	<i>Waste Management</i>	55
7.6	ENVIRONMENTAL SITE INSPECTION	56
7.7	ENVIRONMENTAL NON-CONFORMANCE	56
7.7.1	<i>Summary of Monitoring Exceedance</i>	56
7.7.2	<i>Summary of Environmental Non-Compliance</i>	56
7.7.3	<i>Summary of Environmental Complaint</i>	56
7.7.4	<i>Summary of Environmental Summon and Successful Prosecution</i>	57
7.8	FUTURE KEY ISSUES	57
7.8.1	<i>Key Issues for the Coming Month</i>	57
7.8.2	<i>Monitoring Schedule for the Next Month</i>	57
7.8.3	<i>Construction Programme for the Next Month</i>	57
8	CONCLUSIONS	58

8.1	<i>NORTH POINT PRODUCTION AND DROP SHAFTS</i>	58
8.2	<i>WAN CHAI EAST PRODUCTION AND DROP SHAFTS</i>	58
8.3	<i>CENTRAL DROP SHAFT</i>	58
8.4	<i>SAI YING PUN JUNCTION SHAFT</i>	59
8.5	<i>STONECUTTERS ISLAND PRODUCTION AND RISER SHAFTS</i>	59
8.6	<i>OVERALL</i>	59

## **LIST OF TABLES**

- Table 2.1 *Summary of Environmental Licensing, Notification and Permit Status for the Contract (a)*
- Table 2.2 *Status of Required Submission for all Sites*
- Table 3.1 *Summary of Construction Activities Undertaken from 1 to 30 September 2012 at North Point Production and Drop Shafts*
- Table 3.2 *Summary of Environmental Licensing, Notification and Permit Status at North Point Production and Drop Shafts*
- Table 3.3 *Construction Phase Air Monitoring Location at North Point Production and Drop Shafts*
- Table 3.4 *TSP Monitoring Parameter and Frequency*
- Table 3.5 *TSP Monitoring Equipment for North Point Production and Drop Shafts Sites*
- Table 3.6 *Action and Limit Levels for Air Quality at North Point Production and Drop Shafts*
- Table 3.7 *Construction Phase Noise Monitoring Station at North Point Production and Drop Shafts*
- Table 3.8 *Noise Monitoring Equipment at North Point Production and Drop Shafts*
- Table 3.9 *Action and Limit Levels for Noise Monitoring at North Point Production and Drop Shafts*
- Table 3.10 *Quantities of Waste Generated from the Project for all Sites*
- Table 3.11 *Construction Works to be Undertaken in the Coming Two Months at North Point Production and Drop Shafts*
- Table 4.1 *Summary of Construction Activities Undertaken from 1 to 30 September 2012 at Wan Chai East Production and Drop Shafts*
- Table 4.2 *Summary of Environmental Licensing, Notification and Permit Status at Wan Chai East Production and Drop Shafts*
- Table 4.3 *Construction Phase Air Monitoring Location at Wan Chai East Production and Drop Shafts*
- Table 4.4 *TSP Monitoring Parameter and Frequency at Wan Chai East Production and Drop Shafts*
- Table 4.5 *TSP Monitoring Equipment at Wan Chai East Production and Drop Shafts*
- Table 4.6 *Action and Limit Levels for Air Quality at Wan Chai East Production and Drop Shafts*
- Table 4.8 *Noise Monitoring Equipment at Wan Chai East Production and Drop Shafts*
- Table 4.9 *Action and Limit Levels for Noise Monitoring at Wan Chai East Production and Drop Shafts*
- Table 4.10 *Quantities of Waste Generated from the Project for all Sites*
- Table 4.11 *Summary of Record of Exceedance at Wan Chai East Production and Drop Shafts*
- Table 4.12 *Construction Works to be Undertaken in the Coming Two Months at*

*Wan Chai East Production and Drop Shafts*

<i>Table 5.1</i>	<i>Summary of Construction Activities Undertaken from 1 to 30 September 2012 at Central Drop Shaft</i>
<i>Table 5.2</i>	<i>Summary of Environmental Licensing, Notification and Permit Status at Central Drop Shaft</i>
<i>Table 5.3</i>	<i>Construction Phase Air Monitoring Location at Central Drop Shaft</i>
<i>Table 5.4</i>	<i>TSP Monitoring Parameter and Frequency at Central Drop Shaft</i>
<i>Table 5.5</i>	<i>TSP Monitoring Equipment at Central Drop Shaft</i>
<i>Table 5.6</i>	<i>Action and Limit Levels for Air Quality at Central Drop Shaft</i>
<i>Table 5.7</i>	<i>Construction Phase Noise Monitoring Station at Central Drop Shaft</i>
<i>Table 5.8</i>	<i>Noise Monitoring Equipment at Central Drop Shaft</i>
<i>Table 5.9</i>	<i>Action and Limit Levels for Noise Monitoring at Central Drop Shaft</i>
<i>Table 5.10</i>	<i>Quantities of Waste Generated from the Project for all Sites</i>
<i>Table 5.11</i>	<i>Construction Works to be Undertaken in the Coming Two Months at Central Drop Shaft</i>
<i>Table 6.1</i>	<i>Summary of Construction Activities Undertaken from 1 to 30 September 2012 at Sai Ying Pun Junction Shaft</i>
<i>Table 6.2</i>	<i>Summary of Environmental Licensing, Notification and Permit Status at Sai Ying Pun Junction Shaft</i>
<i>Table 6.3</i>	<i>Construction Phase Air Monitoring Location at Sai Ying Pun Junction Shaft</i>
<i>Table 6.4</i>	<i>TSP Monitoring Parameter and Frequency at Sai Ying Pun Junction Shaft</i>
<i>Table 6.5</i>	<i>Action and Limit Levels for Air Quality at Sai Ying Pun Junction Shaft</i>
<i>Table 6.6</i>	<i>Construction Phase Noise Monitoring Station at Sai Ying Pun Junction Shaft</i>
<i>Table 6.7</i>	<i>Noise Monitoring Equipment at Sai Ying Pun Junction Shaft</i>
<i>Table 6.8</i>	<i>Action and Limit Levels for Noise Monitoring at Sai Ying Pun Junction Shaft</i>
<i>Table 6.9</i>	<i>Quantities of Waste Generated from the Project for all Sites</i>
<i>Table 6.10</i>	<i>Construction Works to be Undertaken in the Coming Two Months at Sai Ying Pun Junction Shaft</i>
<i>Table 7.1</i>	<i>Summary of Construction Activities Undertaken from 1 to 30 September 2012 at Stonecutters Island Production and Riser Shafts</i>
<i>Table 7.2</i>	<i>Summary of Environmental Licensing, Notification and Permit Status at Stonecutters Island Production and Riser Shafts</i>
<i>Table 7.3</i>	<i>Construction Phase Air Monitoring Location at Stonecutters Island Production and Riser Shafts</i>
<i>Table 7.4</i>	<i>TSP Monitoring Parameter and Frequency at Stonecutters Island Production and Riser Shafts</i>
<i>Table 7.5</i>	<i>TSP Monitoring Equipment at Stonecutters Island Production and Riser Shafts</i>
<i>Table 7.6</i>	<i>Action and Limit Levels for Air Quality at Stonecutters Island Production and Riser Shafts</i>



- Table 7.7 Construction Phase Noise Monitoring Station at Stonecutters Island Production and Riser Shafts*
- Table 7.8 Noise Monitoring Equipment at Stonecutters Island Production and Riser Shafts*
- Table 7.9 Action and Limit Levels for Noise Monitoring at Stonecutters Island Production and Riser Shaft*
- Table 7.10 Quantities of Waste Generated from the Project for all Sites*
- Table 7.11 Construction Works to be Undertaken in the Coming Two Months at Stonecutters Island Production and Riser Shafts*

## **LIST OF ANNEXES**

### **Annex A Location of Works Areas**

### **Annex B Project Organization Chart and Contact Detail**

### **Annex C North Point Production and Drop Shaft**

*Annex C1 Locations of Construction Activities during the Reporting Month*

*Annex C2 Locations of Air Quality and Noise Monitoring Stations*

*Annex C3 Monitoring Schedule of the Reporting Month and Next Month*

*Annex C4 Summary of Implementation Status*

*Annex C5 24-hour and 1-hour averaged TSP Monitoring Results*

*Annex C6 Noise Monitoring Results*

*Annex C7 Cumulative Complaint and Summons/Prosecutions Log*

*Annex C8 Construction Programme for the Project*

### **Annex D Wan Chai East Production and Drop Shaft**

*Annex D1 Locations of Construction Activities during the Reporting Month*

*Annex D2 Locations of Air Quality and Noise Monitoring Stations*

*Annex D3 Monitoring Schedule of the Reporting Month and Next Month*

*Annex D4 Summary of Implementation Status*

*Annex D5 24-hour and 1-hour averaged TSP Monitoring Results*

*Annex D6 Noise Monitoring Results*

*Annex D7 Cumulative Complaint and Summons/Prosecutions Log*

*Annex D8 Construction Programme for the Project*

### **Annex E Central Drop Shaft**

*Annex E1 Locations of Construction Activities during the Reporting Month*

*Annex E2 Locations of Air Quality and Noise Monitoring Stations*

*Annex E3 Monitoring Schedule of the Reporting Month and Next Month*

*Annex E4 Summary of Implementation Status*

*Annex E5 24-hour and 1-hour averaged TSP Monitoring Results*

*Annex E6 Noise Monitoring Results*

*Annex E7 Cumulative Complaint and Summons/Prosecutions Log*

*Annex E8 Construction Programme for the Project*

### **Annex F Sai Ying Pun Junction Shaft**

*Annex F1 Locations of Construction Activities during the Reporting Month*

*Annex F2 Locations of Air Quality and Noise Monitoring Stations*

*Annex F3 Monitoring Schedule of the Reporting Month and Next Month*

*Annex F4 Summary of Implementation Status*

*Annex F5 24-hour and 1-hour averaged TSP Monitoring Results*

*Annex F6 Noise Monitoring Results*

*Annex F7 Cumulative Complaint and Summons/Prosecutions Log*

*Annex F8 Construction Programme for the Project*

<b>Annex G</b>	<b>Stonecutters Island Production and Riser Shaft</b>
<i>Annex G1</i>	<i>Locations of Construction Activities during the Reporting Month</i>
<i>Annex G2</i>	<i>Locations of Air Quality and Noise Monitoring Stations</i>
<i>Annex G3</i>	<i>Monitoring Schedule of the Reporting Month and Next Month</i>
<i>Annex G4</i>	<i>Summary of Implementation Status</i>
<i>Annex G5</i>	<i>24-hour and 1-hour averaged TSP Monitoring Results</i>
<i>Annex G6</i>	<i>Noise Monitoring Results</i>
<i>Annex G7</i>	<i>Cumulative Complaint and Summons/Prosecutions Log</i>
<i>Annex G8</i>	<i>Construction Programme for the Project</i>
<b>Annex H</b>	<b>Calibration Reports for HVSSs and Sound Level Meters for All Sites</b>
<b>Annex I</b>	<b>Event /Action Plans for Air Quality, Noise and Landscape and Visual Monitoring</b>
<b>Annex J</b>	<b>Waste Flow Table for All Sites</b>

## ***EXECUTIVE SUMMARY***

The construction works of **DC/2007/23 of Harbour Area Treatment Scheme Stage 2A (HATS2A) - Construction of Sewage Conveyance System from North Point to Stonecutters Island (the Project)** commenced on 1 December 2009. This is the 34<sup>th</sup> monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A activities carried out during the period from 1 to 30 September 2012 in accordance with the EM&A Manual.

## North Point Production and Drop Shafts

### Summary of Construction Works undertaken during the Reporting Month

The major construction works undertaken during the reporting month include:

- Drop Shaft works site has been handed over to Contract DC/2009/23;
- Pumping system, ventilation system and service installation at Production Shaft;
- Chiller installation and commission at Production Shaft; and
- Tunnel communication system installation at Production Shaft.

### Environmental Monitoring and Audit Progress

A summary of the monitoring activities in this reporting period is listed below:

- 24-hour averaged TSP Monitoring at each monitoring station (AM1 and AM2) 5 sets
- 1-hour averaged TSP Monitoring at each monitoring station (AM1 and AM2) 15 sets
- Construction Noise Monitoring during Normal Weekdays at NM1 4 times
- Construction Noise Monitoring during Restricted Hours at NM1 5 times
- Joint Environmental Site Inspection 4 times
- Landscape & Visual Monitoring 1 time

### Air Quality

5 sets of 24-hour average TSP and 15 sets of 1-hr averaged TSP measurements were carried out at each of the designated monitoring stations during the reporting period. No exceedance was recorded during the reporting period.

### Noise

4 sets of 30-minute construction noise measurements were carried out at the monitoring station NM1 during normal weekdays of the reporting period. 5 sets of 3 x 5-minute construction noise measurements were carried out during restricted hours (between 0700 and 2300 hours on Sundays and public holidays) during the reporting month. No Exceedance of the limit level was recorded during normal working hours and restricted hours.

### Landscape & Visual

Landscape and visual monitoring commenced in December 2009. Details of the audit findings and implementation status are presented in *Section 3.5.3*.

### Cultural Heritage

No vibration monitoring was required to be conducted for this reporting month as the blasting of tunnel / shaft works has not started.

### Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. A total of 13,158.97 tonnes of inert C&D materials and 28.5 tonnes of non-inert C&D materials were generated during the reporting period. 400 litres of chemical waste was generated during reporting period. No marine deposit requiring type 1, 2, or 3 disposal methods was generated during the reporting period. Non-inert C&D materials are made up of general refuse, steel materials and paper/cardboard packaging materials. The inert C&D materials and general refuse generated from the Project were disposed of at the Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/Chai Wan Barging Point and SENT Landfill, respectively. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

### Environmental Site Inspection

Four weekly joint environmental site inspections were carried out by the representatives of the Contractor, the Engineer and Environmental Team (ET). Details of the audit findings and implementation status are presented in *Section 3.6*.

### Environmental Exceedance/Non-conformance/Complaint/Summons and Prosecution

No exceedance of Action and Limit Levels of 1-hr and 24-hr TSP was recorded during the reporting period.

No exceedance of Action and Limit Levels of construction noise was recorded during the reporting period.

No non-compliance event was recorded during the reporting period.

No environmental complaint and summon/prosecution was received in this reporting period.

### Future Key Issues

Works to be undertaken in the next two months include:

- Drop Shaft works site has been handed over to Contract DC/2009/23; and
- Installation of Tunnel Services at Production shaft.

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoffs and waste management.

## *Wan Chai East Production and Drop Shafts*

### Summary of Construction Works undertaken during Reporting Month

The major construction works undertaken during the reporting month include:

- Conducting pilot drilling at Drop shaft
- Construction of 2<sup>nd</sup> access gate at Wan Shing Street for Production shaft; and
- Tunnel communication system installation at Production shaft.

### Environmental Monitoring and Audit Progress

A summary of the monitoring activities in this reporting period is listed below:

- |  |         |
|--|---------|
| • 24-hour averaged TSP Monitoring at AM3                       | 6 sets  |
| • 1-hour averaged TSP Monitoring at AM3                        | 18 sets |
| • Construction Noise Monitoring during Normal Weekdays at NM2  | 4 times |
| • Construction Noise Monitoring during Restricted hours at NM2 | 5 times |
| • Joint Environmental Site Inspection                          | 4 times |
| • Landscape & Visual Monitoring                                | 1 time  |

### Air Quality

6 sets of 24-hour average TSP and 18 sets of 1-hr TSP measurements were carried out at the designated monitoring station during the reporting period. No exceedance was recorded during the reporting period.

### Noise

4 sets of 30-minute construction noise measurements were carried out at the monitoring station NM2 during normal weekdays of the reporting period. 5 sets of 3 x 5-minute construction noise measurements were carried out during restricted hours (between 0700 and 2300 hours on Sundays and public holidays) during the reporting month. Exceedance of the limit level was recorded during restricted hour on 25 and 30 September 2012.

### Landscape & Visual

Landscape and visual monitoring commenced in December 2009. Details of the audit findings and implementation status are presented in *Section 4.5.3*.

### Cultural Heritage

No vibration monitoring was required to be conducted for this reporting month as the blasting of tunnel / shaft works was not carried out in the vicinity of the historical buildings mentioned in the EM&A Manual.

### Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. A total of 13,158.97 tonnes of inert C&D materials and 28.5 tonnes of non-inert C&D materials were generated during the reporting period. 400 litres of chemical waste was generated during reporting period. No marine deposit requiring type 1, 2, or 3 disposal methods was generated during the reporting period. Non-inert C&D materials are made up of general refuse, steel materials and paper/cardboard packaging materials. The inert C&D materials and general refuse generated from the Project were disposed of at the Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/Chai Wan Barging Point and SENT Landfill, respectively. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

### Environmental Site Inspection

Four weekly joint environmental site inspections were carried out by the representatives of the Contractor, the Engineer and Environmental Team (ET). Details of the audit findings and implementation status are presented in *Section 4.6*.

### Environmental Exceedance/Non-conformance/Complaint/Summons and Prosecution

No exceedance of Action and Limit Levels of 1-hr and 24-hr TSP was recorded during the reporting period.

Exceedance of noise limit level during restricted hour was reported at NM2 on 25 and 30 September 2012. Investigation into the incident was made and concluded that the ambient traffic noise was the major cause of the noise exceedance recorded on both measurement period during restricted hour. However, the Contractor of this Project was reminded to adhere strictly to the Construction Noise Mitigation Plan and to implement all relevant noise mitigation measures recommended or specified in the EIA, EM&A Manual, EMP, Method Statements, General and Particular Specifications of this Project to avoid exceedance of noise limit levels or causing noise nuisance.

No non-compliance event was recorded during the reporting period.

No environmental complaint and summon/prosecution was received in this reporting period.

No summon/prosecution was received in this reporting period.

### Future Key Issues

Works to be undertaken in the next two months include:

- Raise boring at Drop Shaft; and
- Installation of Tunnel Services at Production Shaft.



Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoffs and waste management.

## Central Drop Shaft

### Summary of Construction Works undertaken during Reporting Month

The major construction works undertaken during the reporting month include:

- General site clean work. .

### Environmental Monitoring and Audit Progress

A summary of the monitoring activities in this reporting period is listed below:

- |   |         |
|---|---------|
| • 24-hour averaged TSP Monitoring at AM4_2                    | 6 sets  |
| • 1-hour averaged TSP Monitoring at AM4_2                     | 18 sets |
| • Construction Noise Monitoring during Normal Weekdays at NM3 | 4 times |
| • Joint Environmental Site Inspection                         | 3 times |
| • Landscape & Visual Monitoring                               | 1 time  |

### Air Quality

6 sets of 24-hour average TSP and 18 sets of 1-hr averaged TSP measurements were carried out at the designated monitoring station during the reporting period. No exceedance was recorded during the reporting period.

### Noise

4 sets of 30-minute construction noise measurements were carried out at the monitoring station NM3 during normal weekdays of the reporting period. No exceedance was recorded during the reporting period.

### Landscape & Visual

Landscape and visual monitoring commenced in December 2009. Details of the audit findings and implementation status are presented in *Section 5.5.3*.

### Cultural Heritage

No vibration monitoring was required to be conducted for this reporting month as the blasting of tunnel / shaft works has not started.

### Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. A total of 13,158.97 tonnes of inert C&D materials and 28.5 tonnes of non-inert C&D materials were generated during the reporting period. 400 litres of chemical waste was generated during reporting period. No marine deposit requiring type 1, 2, or 3 disposal methods was generated during the reporting period. Non-inert C&D materials are made up of general refuse, steel materials and paper/cardboard packaging materials. The inert C&D materials and general

refuse generated from the Project were disposed of at the Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/Chai Wan Barging Point and SENT Landfill, respectively. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

#### Environmental Site Inspection

Three weekly joint environmental site inspections were carried out by the representatives of the Contractor, the Engineer and the Environmental Team (ET). Details of the audit findings and implementation status are presented in *Section 5.6*.

#### Environmental Exceedance/Non-conformance/Complaint/Summons and Prosecution

No exceedance was recorded during the reporting period.

No non-compliance event was recorded during the reporting period.

No environmental complaint and summon/prosecution was received in this reporting period.

#### Future Key Issues

Works to be undertaken in the next two months include:

- General site clean work..

## Sai Ying Pun Junction Shaft

### Summary of Construction Works undertaken during Reporting Month

The major construction works undertaken during the reporting month include:

- Pit bottom steelwork, bunton, services and FSD ladderway installation and
- Alimak installation.

### Environmental Monitoring and Audit Progress

A summary of the monitoring activities in this reporting period is listed below:

- |  |         |
|--|---------|
| • 24-hour average TSP Monitoring at AM5                        | 6 sets  |
| • 1-hour average TSP Monitoring at AM5                         | 18 sets |
| • Construction Noise Monitoring during Normal Weekdays at NM4  | 4 times |
| • Construction Noise Monitoring during Restricted hours at NM4 | 5 times |
| • Joint Environmental Site Inspection                          | 3 times |
| • Landscape & Visual Monitoring                                | 1 time  |

### Air Quality

6 sets of 24-hour averaged TSP and 18 sets of 1-hr averaged TSP measurements were carried out at the designated monitoring station during the reporting period. No exceedance was recorded during the reporting period.

### Noise

4 sets of 30-minute construction noise measurements were carried out at the monitoring station NM4 during normal weekdays of the reporting period. 5 sets of 3 x 5-minute construction noise measurements were carried out during restricted hours during reporting month. No exceedances of the limit level was recorded during normal working hours and restricted hours.

### Landscape & Visual

Landscape and visual monitoring commenced in December 2009. Details of the audit findings and implementation status are presented in *Section 6.5.3*.

### Cultural Heritage

No vibration monitoring was required to be conducted for this reporting month as the blasting of tunnel / shaft works has not started.

### Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. A total of 13,158.97 tonnes of inert C&D materials and 28.5 tonnes of non-inert C&D materials were

generated during the reporting period. 400 litres of chemical waste was generated during reporting period. No marine deposit requiring type 1, 2, or 3 disposal methods was generated during the reporting period. Non-inert C&D materials are made up of general refuse, steel materials and paper/cardboard packaging materials. The inert C&D materials and general refuse generated from the Project were disposed of at the Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/Chai Wan Barging Point and SENT Landfill, respectively. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

#### Environmental Site Inspection

Three weekly joint environmental site inspections were carried out by the representatives of the Contractor, the Engineer and Environmental Team (ET). Details of the audit findings and implementation status are presented in *Section 6.6*.

#### Environmental Exceedance/Non-conformance/Complaint/Summons and Prosecution

No exceedance of Action and Limit Levels of 1-hr and 24-hr TSP was recorded during the reporting period.

No exceedance of Action and Limit Levels of construction noise was recorded during the reporting period.

No non-compliance event was recorded during the reporting period.

No environmental complaint and summon/prosecution was received in this reporting period.

#### Future Key Issues

Works to be undertaken in the next two months include:

- Installation of Tunnel Services; and
- Rail track installation.

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoffs and waste management.

## *Stonecutters Island Production and Riser Shafts*

### Summary of Construction Works undertaken during the Reporting Month

The major construction works undertaken during the reporting month include:

- Shaft steel work installation at Production shaft;
- Alimak installation at Production shaft; and
- Pre-excavation grouting at Riser shaft.

### Environmental Monitoring and Audit Progress

A summary of the monitoring activities in this reporting period is listed below:

- |  |         |
|--|---------|
| • 24-hour averaged TSP Monitoring at AM6                       | 5 sets  |
| • 1-hour averaged TSP Monitoring at AM6                        | 15 sets |
| • Construction Noise Monitoring during Normal Weekdays at NM5  | 4 times |
| • Construction Noise Monitoring during Restricted Hours at NM5 | 4 times |
| • Joint Environmental Site Inspection                          | 4 times |
| • Landscape & Visual Monitoring                                | 1 time  |

### Air Quality

5 sets of 24-hour averaged TSP and 15 sets of 1-hr averaged TSP measurements were carried out at the designated monitoring station during the reporting period. No exceedance was recorded during the reporting period.

### Noise

4 sets of 30-minute construction noise measurements were carried out at the monitoring station NM5 during normal weekdays of the reporting period. 4 sets of 3 x 5-minute construction noise measurements were carried out during restricted hours during reporting month. No exceedance of the limit level was recorded during normal working hours and restricted hours.

### Landscape & Visual

Landscape and visual monitoring commenced in December 2009. Details of the audit findings and implementation status are presented in *Section 7.5.3*.

### Cultural Heritage

No vibration monitoring was required to be conducted for this reporting month as the blasting of tunnel / shaft works has not started.

### Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. A total of 13,158.97 tonnes of inert C&D materials and 28.5 tonnes of non-inert C&D materials were generated during the reporting period. 400 litres of chemical waste was generated during reporting period. No marine deposit requiring type 1, 2, or 3 disposal methods was generated during the reporting period. Non-inert C&D materials are made up of general refuse, steel materials and paper/cardboard packaging materials. The inert C&D materials and general refuse generated from the Project were disposed of at the Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/Chai Wan Barging Point and SENT Landfill, respectively. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

### Environmental Site Inspection

Four weekly joint environmental site inspections were carried out by the representatives of the Contractor, the Engineer and Environmental Team (ET). Details of the audit findings and implementation status are presented in *Section 7.6*.

### Environmental Exceedance/Non-conformance/Complaint/Summons and Prosecution

No exceedance of Action and Limit Levels of 1-hr and 24-hr TSP was recorded during the reporting period.

No exceedance of Action and Limit Levels of construction noise was recorded during the reporting period.

No non-compliance event was recorded during the reporting period.

No environmental complaint and summon/prosecution was received in this reporting period.

### Future Key Issues

Works to be undertaken in the next two months include:

- Installation of tunnel services at Production Shaft; and
- Pre-excavation grouting at Riser Shaft.

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoffs and waste management.

ERM-Hong Kong, Limited (ERM) has been appointed by Gammon Construction Limited (the Contractor) as the Environmental Team (ET) to undertake an Environmental Monitoring and Audit (EM&A) programme for the Contract - No. DC/2007/23 of Harbour Area Treatment Scheme Stage 2A (HATS2A) - Construction of Sewage Conveyance System from North Point to Stonecutters Island (the Project).

### **1.1 PURPOSE OF THE REPORT**

This is the 34<sup>th</sup> EM&A report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from **1 to 30 September 2012**.

### **1.2 STRUCTURE OF THE REPORT**

The structure of the report is as follows:

#### **Section 1 : Introduction**

It details the scope and structure of the report.

#### **Section 2 : Project Information**

It summarises background and scope of the project, site description, project organization and contact details

#### **Section 3 : North Point Production and Drop Shafts**

- **Construction Activities**

It summarises the construction activities conducted during the reporting month.

- **Status of Environmental Approval Documents**

It summarises the environmental documents submissions under the EP condition during the reporting month.

- **Environmental Monitoring Requirement**

It summarises the environmental monitoring including monitoring parameters, programmes, methodologies, frequency, and locations, Action and Limit Levels, Event and Action Plans, environmental mitigation measures as recommended in the EIA report and relevant environmental requirements.

- **Implementation Status on Environmental Mitigation Measures**

It summarises the implementation of environmental protection measures during the reporting period.

- **Monitoring Results**

It summarises the monitoring results obtained in the reporting period.

- **Environmental Site Inspection**



It summarises the audit findings of the weekly site inspections undertaken within the reporting period.

- **Environmental Non-conformance**  
It summarises any monitoring exceedance, environmental complaints and summons within the reporting period.
- **Future Key Issues**  
It summarises the impact forecast and monitoring schedule for the next three months.

#### **Section 4 : Wan Chai East Production and Drop Shafts**

- **Construction Activities**  
It summarises the construction activities conducted during the reporting month.
- **Status of Environmental Approval Documents**  
It summarises the environmental documents submitted under the EP condition during the reporting month.
- **Environmental Monitoring Requirement**  
It summarises the environmental monitoring including monitoring parameters, programmes, methodologies, frequency, and locations, Action and Limit Levels, Event and Action Plans, environmental mitigation measures as recommended in the EIA report and relevant environmental requirements.
- **Implementation Status on Environmental Mitigation Measures**  
It summarises the implementation of environmental protection measures during the reporting period.
- **Monitoring Results**  
It summarises the monitoring results obtained in the reporting period.
- **Environmental Site Inspection**  
It summarises the audit findings of the weekly site inspections undertaken within the reporting period.
- **Environmental Non-conformance**  
It summarises any monitoring exceedance, environmental complaints and summons within the reporting period.
- **Future Key Issues**  
It summarises the impact forecast and monitoring schedule for the next three months.

#### **Section 5 : Central Drop Shaft**

- **Construction Activities**  
It summarises the construction activities conducted during the reporting month.
- **Status of Environmental Approval Documents**  
It summarises the environmental documents submitted under the EP condition during the reporting month.
- **Environmental Monitoring Requirement**  
It summarises the environmental monitoring including monitoring parameters, programmes, methodologies, frequency, and locations, Action and Limit Levels, Event and Action Plans,

environmental mitigation measures as recommended in the EIA report and relevant environmental requirements.

- **Implementation Status on Environmental Mitigation Measures**  
It summarises the implementation of environmental protection measures during the reporting period.
- **Monitoring Results**  
It summarises the monitoring results obtained in the reporting period.
- **Environmental Site Inspection**  
It summarises the audit findings of the weekly site inspections undertaken within the reporting period.
- **Environmental Non-conformance**  
It summarises any monitoring exceedance, environmental complaints and summons within the reporting period.
- **Future Key Issues**  
It summarises the impact forecast and monitoring schedule for the next three months.

#### **Section 6 : Sai Ying Pun Junction Shaft**

- **Construction Activities**  
It summarises the construction activities conducted during the reporting month.
- **Status of Environmental Approval Documents**  
summarises the environmental documents submissions under the EP condition during the reporting month.
- **Environmental Monitoring Requirement**  
It summarises the environmental monitoring including monitoring parameters, programmes, methodologies, frequency, and locations, Action and Limit Levels, Event and Action Plans, environmental mitigation measures as recommended in the EIA report and relevant environmental requirements.
- **Implementation Status on Environmental Mitigation Measures**  
It summarises the implementation of environmental protection measures during the reporting period.
- **Monitoring Results**  
It summarises the monitoring results obtained in the reporting period.
- **Environmental Site Inspection**  
It summarises the audit findings of the weekly site inspections undertaken within the reporting period.
- **Environmental Non-conformance**  
It summarises any monitoring exceedance, environmental complaints and summons within the reporting period.
- **Future Key Issues**  
It summarises the impact forecast and monitoring schedule for the next three months.

#### **Section 7 : Stonecutters Island Production and Riser Shafts**

- **Construction Activities**

It summarises the construction activities conducted during the reporting month.

- **Status of Environmental Approval Documents**

It summarises the environmental documents submitted under the EP condition during the reporting month.

- **Environmental Monitoring Requirement**

It summarises the environmental monitoring including monitoring parameters, programmes, methodologies, frequency, and locations, Action and Limit Levels, Event and Action Plans, environmental mitigation measures as recommended in the EIA report and relevant environmental requirements.

- **Implementation Status on Environmental Mitigation Measures**

It summarises the implementation of environmental protection measures during the reporting period.

- **Monitoring Results**

It summarises the monitoring results obtained in the reporting period.

- **Environmental Site Inspection**

It summarises the audit findings of the weekly site inspections undertaken within the reporting period.

- **Environmental Non-conformance**

It summarises any monitoring exceedance, environmental complaints and summons within the reporting period.

- **Future Key Issues**

It summarises the impact forecast and monitoring schedule for the next three months.

## **Section 8 : Conclusions**

### 2.1 BACKGROUND AND GENERAL SITE DESCRIPTION

The Project comprises the construction of production shafts, drop shafts and riser shaft and approximately 12 km of tunnel excavation from North Point via Sai Ying Pun to Stonecutters Island. Shafts with 10 – 12 m diameter vary in depth from 140 m and 170 m below ground. Tunnel face area ranges from 16 m<sup>2</sup> to 23 m<sup>2</sup>. Embedded drainage pipelines will be installed upon the completion of tunnel excavation.

Construction works to be carried out under this Contract include the following major items:

- construction of sewage conveyance system (SCS) from North Point Preliminary Treatment Works (NP PTW) to Stonecutters Island Sewage Treatment Works (SCI STW) via Wan Chai East Preliminary Treatment Works (WCE PTW), Central Preliminary Treatment Works (CEN PTW) and Fung Mat Street Sai Ying Pun (SYP) junction shaft;
- construction of drop shafts at NP PTW, WCE PTW and CEN PTW;
- construction of riser shaft at SCI STW;
- construction of junction shaft at SYP;
- construction of temporary production shafts at NP, WCE and SCI to provide access for the construction of SCS;
- construction of connection channels, pipes, chambers and tunnel connecting the proposed drop shafts / riser shaft to the facilities of the preliminary treatment works / sewage treatment works;
- carrying out survey of existing buildings, taking over of existing and installation of new piezometers and ground settlement markers and subsequent monitoring thereof and vibration monitoring along the alignment of the SCS;
- miscellaneous building, civil, electrical and mechanical works; and
- landscape works.

The potential environmental impacts of the Project have been studied in the “Harbour Area Treatment Scheme (HATS) Stage 2A” (EIAO Register No: AEIAR-121/2008). The EIA was approved on 2 June 2008 under the *Environmental Impact Assessment Ordinance* (EIAO) and an updated Environmental Permit (EP-322/2008/E) for the works was granted on 24 November 2010. Under the requirements of Condition 4.1 of Environmental Permit EP-322/2008/E,

EM&A programme as set out in the EM&A Manual is required to be implemented.

The construction works of this Project commenced on 1 December 2009 and are scheduled to be completed by 2014.

The general layout plan of the Project is shown in *Annex A*.

## 2.2 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS AND REQUIRED SUBMISSIONS

A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project since December 2009 is presented in *Table 2.1*.

*Table 2.1 Summary of Environmental Licensing, Notification and Permit Status for the Contract <sup>(a)</sup>*

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Environmental Permit	EP-322/2008	Expired on 10 July 2009	<ul style="list-style-type: none"> <li>Permit granted on 19 November 2008</li> <li>Superseded on 10 July 2009</li> </ul>
	EP-322/2008/A	Expired on 2 November 2009	<ul style="list-style-type: none"> <li>Permit granted on 10 July 2009</li> <li>Superseded on 2 November 2009</li> </ul>
	EP-322/2008/B	Expired on 14 May 2010	<ul style="list-style-type: none"> <li>Permit granted on 2 November 2009</li> <li>Superseded on 14 May 2010</li> </ul>
	EP-322/2008/C	Expired on 14 July 2010	<ul style="list-style-type: none"> <li>Permit granted on 14 May 2010</li> <li>Superseded on 14 July 2010</li> </ul>
	EP-322/2008/D	Expired on 24 November 2010	<ul style="list-style-type: none"> <li>Permit granted on 14 July 2010</li> <li>Superseded on 24 November 2010</li> </ul>
	EP-322/2008/E	Throughout the Contract	<ul style="list-style-type: none"> <li>Permit granted on 24 November 2010</li> </ul>
Notification of Construction Works under Air Pollution Control APC (Construction Dust) Regulation	--	04 August 2009 – 06 November 2013	<ul style="list-style-type: none"> <li>Reference number for Notification Pursuant to APC (Construction Dust) Regulation: 308136</li> </ul>
<b>Marine Dumping Permits <sup>(b)</sup></b>			
Type 1 Marine Deposit	EP/MD/11-136	20 February 2011 – 29 June 2011	-
Type 2 Marine Deposit	EP/MD/11-118	20 February 2011 – 21 April 2011	-
Type 3 Marine	8771	23 July 2010 – 22	-

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Deposit		January 2011	

**Notes:**

- (a) The status on environmental licensing and permit for each worksite is discussed in the following sections.
- (b) Marine deposits from all sites have been disposed of in accordance with their respective disposal methods (ie Type 1, 2, or 3 disposal methods), and no further marine deposit is anticipated to generate. When marine deposits are encountered, relevant dumping permits will be obtained and they will be disposed of properly.

Status of required submissions under the EP during the reporting period is presented in *Table 2.2*.

**Table 2.2** *Status of Required EP Submission for all Sites*

EP Condition	Submission	Submission Date
Condition 4.4	Submission of Thirty-third Monthly EM&A Report	14 September 2012

### 2.3 **PROJECT ORGANISATION**

The project organization chart and contact details are shown in *Annex B*.

### 3.1 CONSTRUCTION ACTIVITIES DURING THE REPORTING MONTH

A summary of the major construction activities undertaken in this reporting period is shown in *Table 3.1*. The locations of the construction activities are shown in *Annex C1*.

**Table 3.1** *Summary of Construction Activities Undertaken from 1 to 30 September 2012 at the North Point Production and Drop Shafts*

Worksite	Construction Activities Undertaken
Production Shaft	<ul style="list-style-type: none"> <li>• Pumping system, ventilation system and service installation;</li> <li>• Tunnel communication system installation; and</li> <li>• Chiller installation and commission.</li> </ul>
Drop Shaft	<ul style="list-style-type: none"> <li>• Handed over to Contract no. DC/2009/23.</li> </ul>

### 3.2 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project since December 2009 is presented in *Table 3.2*.

**Table 3.2** *Summary of Environmental Licensing, Notification and Permit Status at North Point Production and Drop Shafts*

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Wastewater Discharge License	North Point PTW Drop Shaft	12 October 2009 - 31 October 2014	--
	WT00005153-2009		
	North Point Production Shaft	9 July 2010 - 31 March 2015	--
Chemical Waste Producer Registration	North Point Production Shaft	--	--
	5213-153-G2484-01		
	North Point PTW Drop Shaft	--	--
Construction Noise Permit CNP	North Point Production shaft	15 March 2011 – 14 September 2012	Replaced by GW-RW0827-12
	GW-RS0234-12		
	North Point Production shaft	14 September 2012 – 13 March 2013	--
	GW-RW0827-12		
	North Point PTW Drop Shaft	23 February 2012 – 22 August 2012	Expired. No CNP is required as no works will take place during restricted hours.
	GW-0101-12		

### 3.3 ENVIRONMENTAL MONITORING REQUIREMENTS

#### 3.3.1 Air Quality Monitoring

##### *Monitoring Location*

In accordance with the EM&A Manual, 24-hour and 1-hour average Total Suspended Particulates (TSP) levels should be conducted at designated monitoring stations. Since access to some of the proposed monitoring locations stated in the EM&A Manual were denied or not available, alternative locations, therefore, were proposed and agreed by the Engineer Representative (ER) and the Independent Environmental Checker (IEC). Due to security issue of the High Volume Sampler (HVS) mounted on the existing monitoring location (rooftop of Water Supplies Department office) especially under adverse weather conditions, an alternative location, which is one floor below the existing rooftop was identified and agreed with the ER and IEC in July 2010.

The construction air quality monitoring stations for this Contract are listed in Table 3.3 and shown in Annex C2.

**Table 3.3 Construction Phase Air Monitoring Location at North Point Production and Drop Shafts**

Worksite	Construction Air Quality Monitoring Stations			
	ID in EM&A Manual	ID	Location	Remark
North Point	-	AM1	Chan's Creative School (formerly known as Madam Chan Wai Chow Memorial School)	• Access for station setup to K.Wah Centre (CM_NP1) and Tin Chiu Street Children's Playground (CM_NP3) was rejected.
	CM_NP2	AM2	Hong Kong & Islands Regional Office, Water Supplies Department	

##### *Monitoring Parameters, Frequency and Programme*

Air quality monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual (Table 3.4). The monitoring programme for this reporting period is shown in Annex C3.

**Table 3.4 TSP Monitoring Parameter and Frequency**

Parameter	Frequency
24-hour average TSP	Once in every 6 days
1-hour average TSP	3 times in every 6 days

##### *Monitoring Equipment*

Continuous 24-hour averaged and three 1-hour averaged TSP monitoring were performed using High Volume Samplers (HVS) with appropriate sampling inlets installed and located at the designated monitoring stations. The performance specification of HVS complied with the standard method



“Determination of Suspended Particulate Matter in the Atmosphere (High Volume Method)” as stipulated in US EPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50 Appendix B). Table 3.5 summarises the equipment that were deployed for the 24-hour and 1-hour averaged TSP monitoring respectively.

**Table 3.5 TSP Monitoring Equipment for North Point Production and Drop Shafts Sites**

Monitoring Station	Monitoring Equipment (HVS and Calibrator)
<i>24-hr and 1-hr TSP</i>	
AM1	GMW GS-2310 (S/N 1808), CM-AIR-43 (S/N 0438320)
AM2	GMW GS-2310 (S/N 0145), CM-AIR-43 (S/N 0438320)

### *Monitoring Methodology*

#### Installation

The setup locations of the HVSs at monitoring stations were listed in Table 3.3. All HVSs were free-standing with no obstruction.

The following criteria were considered in the installation of the HVSs:

- appropriate support to secure the samplers against gusty wind were provided at AM1 and AM2;
- a minimum of 2 m separation from walls, parapets and penthouses was required for rooftop samplers;
- no furnace or incinerator flues was nearby;
- airflow around the sampler was unrestricted; and
- permission was obtained to set up the samplers and to gain access to the monitoring stations.

#### Preparation of Filter Papers

- glass fibre filters were labelled and sufficient filters that were clean and without pinholes were selected;
- all filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than  $\pm 3$  °C; the relative humidity (RH) was 40%; and
- SGS Hong Kong Ltd, a HOKLAS accredited laboratory, implements comprehensive quality assurance and quality control programmes.

#### Field Monitoring

- the power supply was checked to ensure that the HVSs were working properly;

- the filter holder and the area surrounding the filter were cleaned;
- the filter holder was removed by loosening the four bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully;
- the filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter;
- the swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges;
- the shelter lid was closed and secured with the aluminium strip;
- the HVSs were warmed-up for about 5 minutes to establish run-temperature conditions;
- a new flowrate record sheet was set into the flow recorder;
- the flow rates of the HVSs were checked and adjusted to between 1.22 - 1.37 m<sup>3</sup>min<sup>-1</sup> which were within the range specified in the EM&A Manual (ie 0.6 – 1.7 m<sup>3</sup>min<sup>-1</sup>);
- the programmable timer was set for a sampling period of 24 hours ± 1 hour, and the starting time, weather condition and the filter number were recorded;
- the initial elapsed time was recorded;
- at the end of sampling, the sampled filter was removed carefully and folded in half so that only surfaces with collected particulate matter were in contact;
- the filter paper was then placed in a clean plastic envelope and sealed;
- all monitoring information was recorded on a standard data sheet; and
- filters were sent to SGS Hong Kong Ltd for analysis.

#### Maintenance and Calibration

- the HVSs and their accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply; and
- the flow rate of each HVS with mass flow controller was calibrated using an orifice calibrator. Initial calibrations of the dust monitoring equipments were conducted upon installation and prior to commissioning. Five-point calibration was carried out for HVSs using CM-AIR-43 Calibration Kit. HVSs are calibrated on a bi-monthly basis. The calibration records for the HVSs are given in *Annex H*.

### Wind Data

The nearest weather station to North Point Production and Drop Shafts is Kai Tak Station. Average wind data (wind speed and wind direction) during the monitoring period were obtained from the meteorological station at Kai Tak of the Hong Kong Observatory (HKO) and are presented in *Annex C5*.

### *Action and Limit Levels*

The Action and Limit (A/L) levels have been established and are presented in *Table 3.6*.

**Table 3.6** *Action and Limit Levels for Air Quality at North Point Production and Drop Shafts*

Parameter	Air Monitoring Station	Action Level, $\mu\text{gm}^{-3}$	Limit Level, $\mu\text{gm}^{-3}$
24-hour average TSP	AM1	185	260
	AM2	182	260
1-hour average TSP	AM1	340	500
	AM2	352	500

### *Event and Action Plan*

The Event and Action Plan (EAP) for air quality monitoring is presented in *Annex I*.

### 3.3.2 *Noise Monitoring*

#### *Monitoring Location*

In accordance with the EM&A Manual, monitoring of construction noise impact should be conducted at the designated monitoring stations. Since access to some of the proposed monitoring locations stated in the EM&A Manual was denied or not available; alternative locations were proposed and agreed by the ER and the IEC. Construction activities were conducted at restricted hours (1900 – 2300 on all days and 0700 – 2300 on general holidays and Sundays) during the reporting month. As the constraint of Chan’s Creative School’s schedule (closed from 1900 to 0700 on normal week days and from 0000 to 2400 on public holidays as well as Sundays), the school (noise monitoring station NM1) is not accessible during restricted hours, noise monitoring during restricted hours would be conducted on the pedestrian walkway adjacent to the school boundary along Tin Chiu Street, which was agreed by the ER and the IEC. The construction noise monitoring location for this Contract is listed in *Table 3.7* and is shown in *Annex C2*.

**Table 3.7 Construction Phase Noise Monitoring Station at North Point Production and Drop Shafts**

Worksite	Proposed Construction Noise Monitoring Station				
	ID in EM&A Manual	ID	Location	Type of Measurement	Remark
North Point	M1	NM1	Rooftop of Chan's Creative School (formerly known as Madam Chan Wai Chow Memorial School)	Façade	0700 to 1900 on Monday to Saturday
			Pedestrian walkway adjacent to Chan's Creative School (formerly known as Madam Chan Wai Chow Memorial School) boundary along Tin Chiu Street	Façade	Restricted hours (1900 – 2300 on all days and 0700 – 2300 on general holidays and Sundays)

#### *Monitoring Parameters, Frequency and Programme*

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. Additional noise monitoring were also conducted as per required in the EM&A Manual when works were carried out during restricted periods. The monitoring programme for this reporting period is shown in *Annex C3*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ) in decibels dB(A).  $L_{eq(30min)}$  were used as the monitoring parameter for the period between 0700 – 1900 hours on normal weekdays, and  $L_{eq(5min)}$  were used as the monitoring parameter for all restricted periods. Supplementary information for data auditing (two statistical sound levels  $L_{10}$  and  $L_{90}$  which are the levels exceeded for 10 and 90 percent of the time respectively) were also monitored for reference. The measured noise levels were logged every 5 minutes throughout the impact monitoring period.

#### *Monitoring Equipment and Methodology*

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures of Technical Memorandum on Noise from Construction Work other than Percussive Piling (GW-TM)* issued under the *Noise Control Ordinance (NCO)* (Cap.400).

The sound level meters and calibrator used for the noise measurement, as listed in *Table 3.8*, comply with IEC 651: 1979 and 804:1985 (Type 1) specification. The calibration certificates of the sound level meters are included in *Annex H*.

**Table 3.8 Noise Monitoring Equipment at North Point Production and Drop Shafts**

Monitoring Station	Monitoring Equipment (Sound Level Meter and Calibrator)
NM1	<ul style="list-style-type: none"> <li>• Calibrator: RION - NC73 (S/N 10997142)</li> <li>• Sound Level Meters: Rion NL-52 (S/N 00710259) and Rion NL-31 (S/N 00603867)</li> </ul>

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

*Action and Limit Levels*

The limit levels for noise monitoring during different monitoring periods are summarised in *Table 3.9*.

**Table 3.9 Limit Levels for Noise Monitoring at North Point Production and Drop Shafts**

Noise Monitoring Location	Measurement Parameter	Limit Level (dB(A))	Remark
NM1	L <sub>eq</sub> (30mins)	70	During normal teaching period
	L <sub>eq</sub> (30mins)	69 <sup>(a)</sup>	During the school examination period
	L <sub>eq</sub> (30mins)	75	During school holidays
	L <sub>eq</sub> (5mins)	70	Evening (1900-2300); and Sundays and public holidays (0700-2300)
	L <sub>eq</sub> (5mins)	55	Night-time (2300-0700)

**Note:**

(a) With reference to the Baseline Monitoring Report, the average L<sub>Aeq,30min</sub> measured at NM1 between 0700 and 1900 hours is 69.0 dB(A), exceeding the Limit Level of daytime construction noise during examination periods (65 dB(A)), It will therefore be adopted as the Limit Level during the examination period at NM1.

*Event and Action Plan*

The Event and Action Plan (EAP) for noise monitoring is presented in *Annex I*.

**3.3.3 Cultural Heritage**

No vibration monitoring is required for this reporting month as no blasting of tunnel / shaft works was carried out.

**3.3.4 Landscape and Visual Monitoring**

In accordance with the EM&A Manual, landscape and visual monitoring is required to ensure that the design, implementation and maintenance of landscape and visual mitigation measures are fully achieved. The landscape and visual monitoring was carried out on site within the environmental site inspection. The monitoring procedures and criteria as described in the EM&A Manual were adopted.

## *Event and Action Plan*

The Event and Action Plan (EAP) for landscape and visual monitoring is presented in *Annex I*.

### **3.4 IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS**

The Contractor has implemented environmental mitigation measures and fulfilled requirements as stated in the EIA Report, Environmental Permit and EM&A Manual. The implementation status during the reporting period is summarised in *Annex C4*.

### **3.5 MONITORING RESULTS**

#### **3.5.1 Air Quality**

A total of 5 sets of 24-hour averaged and 15 sets of 1-hour averaged TSP measurements were carried out at AM1 and AM2 respectively during the reporting period. The monitoring data for 24-hour and 1-hour averaged TSP together with wind data and graphical presentations are presented in *Annex C5*.

The weather condition during the monitoring period varied from sunny to cloudy. The local impacts near the monitoring stations of AM1 to AM2 were mainly associated with vehicle emissions. No exceedance of Action and Limit Levels of 1-hr and 24-hr TSP was recorded during the reporting period.

#### **3.5.2 Noise**

A total of 4 sets of 30-minute construction noise measurements were carried out at the monitoring station NM1 during normal weekdays of the reporting period. The local impacts at normal hours during weekdays observed near the monitoring stations of NM1 included traffic noise from King's Road, Java Road and nearby roads; school bell rings; student noise and the construction works by other parties undertaken in the vicinity. No exceedance of limit level for noise monitoring during normal working hours was recorded.

5 sets of 3 x 5-minute construction noise measurements were carried out at NM1 during restricted hours (between 1900 and 0700 hours on weekdays and any time on Sundays and public holidays) on 2, 11, 16, 25 and 30 September 2012. No exceedance of limit level for noise monitoring during restricted hours was recorded. The local impacts during restricted hours observed included traffic noise from King's Road, Java Road and nearby roads and the construction works by other parties undertaken in the vicinity.

The monitoring results together with graphical presentations are presented in *Annex C6*.

### 3.5.3 *Landscape and Visual*

Implementation and maintenance of landscape and visual mitigation measures are fully implemented and no major finding was made during the reporting month.

### 3.5.4 *Cultural Heritage*

No vibration monitoring was conducted for this reporting month as the blasting of tunnel/ shaft works has not commenced.

### 3.5.5 *Waste Management*

Waste generated from this Project includes inert construction and demolition (C&D) materials, non-inert C&D materials, and marine deposit. Non-inert C&D materials are made up of general refuse, steel and paper/cardboard packaging materials. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. No marine deposits requiring Type 1, 2, and 3 disposal methods was generated during the reporting month. Reference has been made to the Monthly Summary Waste Flow Table prepared by the Contractor (*Annex J*). The waste statistics provided in this section represents the cumulative quantity of wastes generated from all sites in this Project. With reference to the relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in *Table 3.10*. The inert C&D materials and general refuse generated from the Project were disposed of at Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/Chai Wan Barging Point and SENT Landfill respectively. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

**Table 3.10** *Quantities of Waste Generated from the Project for all Sites*

Month / Year	Quantity					
	C&D Materials (inert) (a)	C&D Materials (non-inert) (b)	Chemical Waste	Marine Deposit		
				Type 1	Type 2	Type 3
September 2012	13,158.97 tonnes	28.5 tonnes	400 L	0 m <sup>3</sup>	0 m <sup>3</sup>	0 tonnes

**Notes:**

- (a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil. 7,212.5 tonnes of inert C&D materials were disposed of at the Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/ Chai Wan Barging Point and 5,946.47 tonnes of broken rock have been transferred to SENT Landfill for use.
- (b) Non-inert C&D materials include steel, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Steel materials generated from the project are grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. The non-inert C&D materials other than steel and paper/cardboard packaging were disposed of at SENT Landfill. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

### 3.6 ENVIRONMENTAL SITE INSPECTION

Weekly site inspections were carried out by the representatives of the Contractor, the Engineer and the ET. Site inspections were conducted on 6, 13, 20 and 27 September 2012. The representative of the IEC joined the site inspection on 27 September 2012. No non-compliance was recorded during the site inspections.

Major findings and recommendations are summarised as follows:

#### *Production Shaft*

- On 6 September, most of the oil spillage on the ground observed during last month site inspection near the chemical storage area has been removed. The Contractor was reminded to further remove the oil stains.
- On 20 September, oil spillage on the ground was observed near the chemical storage area. The Contractor was reminded to remove the spillage and oil stains by absorbent materials and emulsifiers properly. The Contractor was reminded to ensure the chemical store is totally sealed to avoid any oil spillage or accumulation of water especially during rainy seasons.

#### *Drop Shaft*

- Nil.

### 3.7 ENVIRONMENTAL NON-CONFORMANCE

#### 3.7.1 *Summary of Monitoring Exceedance*

No exceedance of the A/L Levels of 1-hour averaged and 24-hour averaged TSP was recorded at the monitoring stations during the reporting period.

No exceedance of the Noise Limit Levels was recorded at the monitoring station during both normal working hours and restricted hours in the reporting period.

#### 3.7.2 *Summary of Environmental Non-Compliance*

No non-compliance event was recorded during the reporting period.

#### 3.7.3 *Summary of Environmental Complaint*

No complaint was received during the reporting period. The cumulative complaint log is shown in *Annex C7*.

#### 3.7.4 *Summary of Environmental Summon and Successful Prosecution*

No summon was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex C7*.



### 3.8 *FUTURE KEY ISSUES*

#### 3.8.1 *Key Issues for the Coming Months*

Works to be undertaken in the coming two monitoring periods are summarised in *Table 3.11*.

**Table 3.11** *Construction Works to be undertaken in the Coming Two Months at North Point Production and Drop Shafts*

<b>Work to be taken</b>
<i>Production Shaft</i>
<ul style="list-style-type: none"><li>• Installation of Tunnel Services.</li></ul>
<i>Drop Shaft</i>
<ul style="list-style-type: none"><li>• Hand over to Contract DC/2009/23 for pipe laying.</li></ul>

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoffs and waste management.

#### 3.8.2 *Monitoring Schedule for the Next Month*

The tentative schedule of TSP and noise monitoring for the next reporting period is presented in *Annex C3*. Environmental monitoring will be conducted at the same monitoring locations in the reporting period.

#### 3.8.3 *Construction Programme for Next Month*

The most up-to-date construction programme for the Project is presented in *Annex C8*.

#### 4.1 CONSTRUCTION ACTIVITIES DURING THE REPORTING MONTH

A summary of the major construction activities undertaken in this reporting period is shown in *Table 4.1*. The locations of the construction activities are shown in *Annex D1*.

**Table 4.1** *Summary of Construction Activities undertaken from 1 to 30 September 2012 at the Wan Chai East Production and Drop Shafts*

Worksite	Construction Activities Undertaken
Production Shaft	<ul style="list-style-type: none"> <li>Construction of second access gate at Wan Shing Street;</li> <li>Tunnel communication system installation.</li> </ul>
Drop Shaft	<ul style="list-style-type: none"> <li>Conducting pilot drilling.</li> </ul>

#### 4.2 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project since December 2009 is presented in *Table 4.2*.

**Table 4.2** *Summary of Environmental Licensing, Notification and Permit Status at Wan Chai East Production and Drop Shafts*

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Wastewater Discharge License	Wan Chai East Production Shaft and Drop Shaft WT00007023-2010	13 July 2010 - 31 October 2014	Superseded by
	Wan Chai East Production Shaft and Drop Shaft WT00008533-2011	21 February 2011 - 31 October 2014	--
Chemical Waste Producer Registration	Wan Chai East Production Shaft and Drop Shaft 5213-135-G2308-03	--	--
Construction Noise Permit (CNP)	Wan Chai East Production Shaft GW-RS0209-12	27 August 2012 – 26 February 2013	--
	Wan Chai East Drop Shaft GW-RS0801-12	30 July 2012 – 29 January 2013	--

### 4.3 ENVIRONMENTAL MONITORING REQUIREMENTS

#### 4.3.1 Air Quality Monitoring

##### *Monitoring Location*

In accordance with the EM&A Manual, 24-hour and 1-hour averaged Total Suspended Particulates (TSP) levels should be conducted at designated monitoring stations. Since access to some of the proposed monitoring locations stated in the EM&A Manual was denied or not available, alternative locations, therefore, were proposed and agreed by the ER and the IEC. The construction air quality monitoring station for this Contract is listed in *Table 4.3* and shown in *Annex D2*.

**Table 4.3 Construction Phase Air Monitoring Location at Wan Chai East Production and Drop Shafts**

Worksite	Construction Air Quality Monitoring Station			
	ID in EM&A Manual	ID	Location	Remark
Wan Chai East	-	AM3	Rooftop of Wan Chai East PTW	<ul style="list-style-type: none"> <li>The rooftop of the Society for the Prevention of Cruelty to Animals building (CM_WC1) was so crowded with existing facilities (eg water tanks) that the setup of HVSs for baseline monitoring was not feasible.</li> </ul>

##### *Monitoring Parameters, Frequency and Programme*

Air quality monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual (*Table 4.4*). The monitoring programme for this reporting period is shown in *Annex D3*.

**Table 4.4 TSP Monitoring Parameter and Frequency at Wan Chai East Production and Drop Shafts**

Parameter	Frequency
24-hour average TSP	Once in every 6 days
1-hour average TSP	3 times in every 6 days

##### *Monitoring Equipment*

Continuous 24-hour and 1-hour averaged TSP monitoring were performed using High Volume Samplers (HVS) with appropriate sampling inlets installed, located at the designated monitoring station. The performance specification of HVS complied with the standard method "*Determination of Suspended Particulate Matter in the Atmosphere (High Volume Method)*" as stipulated in *US EPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50 Appendix B)*. *Table 4.5* summarises the equipment that was deployed for the 24-hour and 1-hour averaged TSP monitoring.

**Table 4.5 TSP Monitoring Equipment at Wan Chai East Production and Drop Shafts**

Monitoring Station	Monitoring Equipment (HVS and Calibrator)
24-hr and 1-hr TSP	
AM3	GMW GS-2310 (S/N 0481), CM-AIR-43 (S/N 0438320)

*Monitoring Methodology*

Installation

The setup location of the HVS at monitoring stations was listed in *Table 4.3*. The HVS was free-standing with no obstruction.

The following criteria were considered in the installation of the HVSs:

- appropriate support to secure the sampler against gusty wind was provided at AM3;
- a minimum of 2 m separation from walls, parapets and penthouses was required for rooftop samplers;
- no furnace or incinerator flues was nearby;
- airflow around the sampler was unrestricted; and
- permission was obtained to set up the samplers and to gain access to the monitoring stations.

Preparation of Filter Papers

- glass fibre filters were labelled and sufficient filters that were clean and without pinholes were selected;
- all filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than  $\pm 3$  °C; the relative humidity (RH) was 40%; and
- SGS Hong Kong Ltd, a HOKLAS accredited laboratory, implements comprehensive quality assurance and quality control programmes.

Field Monitoring

- the power supply was checked to ensure that the HVSs were working properly;
- the filter holder and the area surrounding the filter were cleaned;
- the filter holder was removed by loosening the foul bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully;

- the filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter;
- the swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges;
- the shelter lid was closed and secured with the aluminium strip;
- the HVSs were warmed-up for about 5 minutes to establish run-temperature conditions;
- a new flow rate record sheet was set into the flow recorder;
- the flow rates of the HVSs were checked and adjusted to between 1.22 - 1.37 m<sup>3</sup>min<sup>-1</sup> which were within the range specified in the EM&A Manual (ie 0.6 – 1.7 m<sup>3</sup>min<sup>-1</sup>);
- the programmable timer was set for a sampling period of 24 hours ± 1 hour, and the starting time, weather condition and filter number were recorded;
- the initial elapsed time was recorded;
- at the end of sampling, the sampled filter was removed carefully and folded in half so that only surfaces with collected particulate matter were in contact;
- the filter paper was then placed in a clean plastic envelope and sealed;
- all monitoring information was recorded on a standard data sheet; and
- filters were sent to SGS Hong Kong Ltd for analysis.

#### Maintenance and Calibration

- the HVSs and their accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply; and
- the flow rate of each HVS with mass flow controller was calibrated using an orifice calibrator. Initial calibrations of the dust monitoring equipments were conducted upon installation and prior to commissioning. Five-point calibration was carried out for HVSs using CM-AIR-43 Calibration Kit. HVSs are calibrated on a bi-monthly basis. The calibration record for the HVS is given in *Annex H*.

#### Wind Data

The nearest weather station to Wan Chai East Production and Drop Shafts is located at King's Park. Average wind data (wind speed and wind direction) during the monitoring period were obtained from the meteorological station

at King's Park of the Hong Kong Observatory (HKO) and are presented in *Annex D5*.

#### *Action and Limit Levels*

The Action and Limit levels have been established and are presented in *Table 4.6*.

**Table 4.6** *Action and Limit Levels for Air Quality at Wan Chai East Production and Drop Shafts*

Parameter	Air Monitoring Station	Action Level, $\mu\text{gm}^{-3}$	Limit Level, $\mu\text{gm}^{-3}$
24-hour average TSP	AM3	181	260
1-hour average TSP	AM3	355	500

#### *Event and Action Plan*

The Event and Action Plan (EAP) for air quality monitoring is presented in *Annex I*.

### 4.3.2 *Noise Monitoring*

#### *Monitoring Location*

In accordance with the EM&A Manual, monitoring of construction noise impact should be conducted at the designated monitoring stations. Since access to some of the proposed monitoring locations stated in the EM&A Manual was denied or not available, alternative locations were proposed and agreed by the ER and the IEC. The construction noise monitoring location for this Contract is listed in *Table 4.7* and shown in *Annex D2*.

**Table 4.7** *Construction Phase Noise Monitoring Station at Wan Chai East Production and Drop Shafts*

Worksite	Construction Noise Monitoring Station				
	ID in EM&A Manual	ID	Location	Type of Measurement	Remark
Wan Chai East	-	NM2	Rooftop of Hyde Building	Façade	<ul style="list-style-type: none"> <li>No guaranteed access for equipment set-up due to the non-existence of a caretaker of Kei Wah Building (M2)</li> <li>Alternative location, NM2, is located next to Kei Wah Building and is also the background noise monitoring station in the HATS2A EIA study.</li> </ul>

### *Monitoring Parameters, Frequency and Programme*

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. Additional noise monitoring was also conducted as per required in the EM&A Manual when works were carried out during restricted periods. The monitoring programme for this reporting period is shown in *Annex D3*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ) in decibels dB(A).  $L_{eq(30min)}$  were used as the monitoring parameter for the time period between 0700 – 1900 hours on normal weekdays, and  $L_{eq(5min)}$  were used as the monitoring parameter for all restricted periods. Supplementary information for data auditing (two statistical sound levels  $L_{10}$  and  $L_{90}$  which are the levels exceeded for 10 and 90 percent of the time respectively) were also recorded during the monitoring period for reference. The measured noise levels were logged every 5 minutes throughout the impact monitoring period.

### *Monitoring Equipment and Methodology*

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures of Technical Memorandum on Noise from Construction Work other than Percussive Piling (GW-TM)* issued under the *Noise Control Ordinance (NCO) (Cap.400)*.

The sound level meters and calibrator used for the noise measurement, as listed in *Table 4.8*, comply with IEC 651: 1979 and 804:1985 (Type 1) specification. The calibration certificates of the sound level meters are included in *Annex H*.

**Table 4.8** *Noise Monitoring Equipment at Wan Chai East Production and Drop Shafts*

<b>Monitoring Station</b>	<b>Monitoring Equipment (Sound Level Meter and Calibrator)</b>
NM2	<ul style="list-style-type: none"><li>• Calibrator: RION - NC73 (S/N 10997142)</li><li>• Sound Level Meters: Rion NL-52 (S/N 00710259) and Rion NL-31 (S/N 00603867)</li></ul>

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

### *Action and Limit Levels*

The limit levels for noise monitoring during different monitoring periods are summarised in *Table 4.9*.

**Table 4.9** *Limit Levels for Noise Monitoring at Wan Chai East Production and Drop Shafts*

Noise Monitoring Location	Measurement Parameter	Limit Level (dB(A))	Remark
NM2	Leq(30mins)	75	Normal working hours during weekdays
	Leq(5mins)	70	Evening (1900-2300); and Sundays and public holidays (0700-2300)
	Leq(5mins)	55	Night-time (2300-0700)

*Event and Action Plan*

The Event and Action Plan (EAP) for noise monitoring is presented in *Annex I*.

**4.3.3** *Cultural Heritage*

No vibration monitoring is required for this reporting month as blasting of tunnel / shaft works was not carried out in the vicinity of the historical buildings mentioned in EM&A manual.

**4.3.4** *Landscape and Visual Monitoring*

In accordance with the EM&A Manual, landscape and visual monitoring is required to ensure that the design, implementation and maintenance of landscape and visual mitigation measures are fully achieved. The landscape and visual monitoring was carried out on site within the environmental site inspection. The monitoring procedures and criteria as described in the EM&A Manual were adopted.

*Event and Action Plan*

The Event and Action Plan (EAP) for landscape and visual monitoring is presented in *Annex I*.

**4.4** *IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS*

The Contractor has implemented environmental mitigation measures and fulfilled the requirements as stated in the EIA Report, Environmental Permit and EM&A Manual. The implementation status during the reporting period is summarised in *Annex D4*.

**4.5** *MONITORING RESULTS*

**4.5.1** *Air Quality*

A total of 6 sets of 24-hour averaged and 18 sets of 1-hour averaged TSP measurements were made at AM3 during the reporting period. The monitoring data for 24-hour and 1-hour average TSP, together with the wind data and graphical presentations, are presented in *Annex D5*.



The weather condition during the monitoring period varied from sunny to cloudy. The local impacts near the monitoring stations of AM3 were mainly associated with vehicle emissions. No exceedance of Action and Limit Levels of 1-hr and 24-hr TSP was recorded during the reporting period.

#### **4.5.2**      *Noise*

A total of 4 sets of 30-minute construction noise measurements were carried out at the monitoring station NM2 during normal working hours in weekdays of the reporting period. No exceedance of limit level for noise monitoring during normal working hours was recorded.

5 sets of 3 x 5-minute construction noise measurements were carried out during restricted hours (between 1900 and 0700 hours on weekdays, and any time on Sundays and public holidays) on 2, 11, 16, 25 and 30 September 2012. Noise level recorded during restricted hour on 25 and 30 September 2012 exceeded the limit level at NM2. Investigation had been conducted to review the potential causes for the noise level recorded. A summary of the investigation result is presented in *Section 4.7.1*.

The monitoring results, together with graphical presentations, are presented in *Annex D6*. The local impacts observed near the monitoring stations of NM2 were due to traffic noise from Gloucester Road and Hung Hing Road.

#### **4.5.3**      *Landscape and Visual*

Implementation and maintenance of landscape and visual mitigation measures are fully achieved and no major finding was made during the reporting month.

#### **4.5.4**      *Cultural Heritage*

No vibration monitoring is required for this reporting month as blasting of tunnel/shaft works was not carried out in the vicinity of the historical buildings mentioned in EM&A manual.

#### **4.5.5**      *Waste Management*

Waste generated from this Project includes inert construction and demolition (C&D) materials, non-inert C&D materials, and marine deposit. Non-inert C&D materials are made up of general refuse, steel and paper/cardboard packaging materials. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. No marine deposits requiring Type 1, 2, and 3 disposal methods was generated during the reporting month. Reference has been made to the Monthly Summary Waste Flow Table prepared by the Contractor (*Annex J*). The waste statistics provided in this section represent the cumulative quantity of wastes generated from all sites in this Project. With reference to the relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in *Table 4.10*. The inert C&D materials and general refuse

generated from the Project were disposed of at Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/Chai Wan Barging Point and SENT Landfill respectively. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

**Table 4.10** *Quantities of Waste Generated from the Project for all Sites*

Month / Year	Quantity					
	C&D Materials (inert) <sup>(a)</sup>	C&D Materials (non-inert) <sup>(b)</sup>	Chemical Waste	Marine Deposit		
				Type 1	Type 2	Type 3
September 2012	13,158.97 tonnes	28.5 tonnes	400 L	0 m3	0 m3	0 tonnes

**Notes:**

(a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil. 7212.5 tonnes of inert C&D materials were disposed of at the Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/ Chai Wan Barging Point and 5946.47 tonnes of broken rock have been transferred to SENT Landfill for use.

(b) Non-inert C&D materials include steel, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Steel materials generated from the project are grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. The non-inert C&D materials other than steel and paper/cardboard packaging were disposed of at SENT Landfill. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

**4.6**

**ENVIRONMENTAL SITE INSPECTION**

Weekly site inspections were carried out by representatives of the Contractor, Engineer and the ET. Site inspections were conducted on 6, 13, 20 and 27 September 2012. The IEC joined in the site inspection on 27 September. There was no non-compliance recorded during the site inspections.

Major findings and recommendations are summarised as follows:

*Production Shaft*

- On 6 September, a truck leaving the site without passing through washing bay was observed during the site inspection. The Contractor was reminded to provide sufficient training and reminders/signage to remind all drivers to wash the trucks before leaving the construction site.
- On 6 September, stagnant water was observed inside the chemical store. The Contractor was reminded to remove the stagnant water properly to avoid mosquito breeding.
- On 20 September, two chemical drums inside the noise enclosure were observed without drip tray. The Contractor was reminded to put the drums on the drip tray and store the chemical drums properly on site.

*Drop Shaft*

- On 27 September, stagnant water was observed in the spare tires under tarpaulin near the drop shaft. The Contractor was reminded to remove the stagnant water to avoid mosquito breeding, especially after rainfall events.

## 4.7 ENVIRONMENTAL NON-CONFORMANCE

### 4.7.1 Summary of Monitoring Exceedance

No exceedance of the A/L Levels of 1-hour and 24-hour averaged TSP was recorded at monitoring stations during the reporting period.

Exceedance of noise limit level during restricted hours was reported at NM2 on 25 and 30 September 2012. Investigation into the incident has been made. It was considered that traffic noise was the major cause of the exceedance recorded and hence is not project related. Although the exceedance was not caused by the Project, the Contractor of this Project was reminded to adhere strictly to the Construction Noise Mitigation Plan and to implement all relevant noise mitigation measures recommended or specified in the EIA, EM&A Manual, EMP, Method Statements, General and Particular Specifications of this Project to avoid exceedance of noise limit levels or causing noise nuisance.

**Table 4.11** *Summary of Record of Exceedance at Wan Chai East Production and Drop Shafts*

Station	Record of Exceedance	Result of Investigation
NM2	Exceedance of Limit Level on 25 September 2012 (20:19 - 20:34)	<p>According to the works summary provided by the Contractor, no works had been performed outside the noise enclosure. Other construction activities that took place during the noise monitoring session included preparing for grouting grout holes No. 95, 96 and 97; laying rail switch and drilling for rail support dowels; survey work and operating winder and gantry. These activities were carried out inside the noise enclosure.</p> <p>It was observed no noisy outdoor construction activities at the Wan Chai East Production and Drop Shafts during the noise monitoring session. This is consistent with the works summary provided by the Contractor showing no major outdoor construction activities that have taken place during the same period.</p> <p>Based on the above, the exceedance observed is considered attributable to the road traffic noise in the vicinity of the Site and is non-project related.</p>

Station	Record of Exceedance	Result of Investigation
NM2	Exceedance of Limit Level on 30 September 2012 (11:28 - 11:43)	<p>According to the works summary provided by the Contractor, no works had been performed outside the noise enclosure. Other construction activities that took place during the noise monitoring session included connecting hydraulic hoses to the grout pump machine; removing concrete at TJ5 Sump Pit; lifting electrical cable to bottom shaft and operating winder and gantry. These activities were carried out inside the noise enclosure.</p> <p>It was observed no noisy outdoor construction activities at the Wan Chai East Production and Drop Shafts during the noise monitoring session. This is consistent with the works summary provided by the Contractor showing no major outdoor construction activities that have taken place during the same period.</p> <p>Based on the above, the exceedance observed is considered attributable to the road traffic noise in the vicinity of the Site and is non-project related.</p>

#### 4.7.2 *Summary of Environmental Non-Compliance*

No non-compliance event was recorded during the reporting period.

#### 4.7.3 *Summary of Environmental Complaint*

No complaint was received during the reporting period. The cumulative complaint log is shown in *Annex D7*.

#### 4.7.4 *Summary of Environmental Summon and Successful Prosecution*

No summons was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex D7*.

### 4.8 *FUTURE KEY ISSUES*

#### 4.8.1 *Key Issues for the Coming Month*

Works to be undertaken for the coming two monitoring periods are summarised in *Table 4.12*.

**Table 4.12. *Construction Works to be Undertaken in the Coming Two Months at Wan Chai East Production and Drop Shafts***

Work to be taken
<i>Production Shaft</i>
<ul style="list-style-type: none"> <li>• Installation of Tunnel Services.</li> </ul>
<i>Drop Shaft</i>
<ul style="list-style-type: none"> <li>• Raise boring</li> </ul>

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoff and waste management.

#### **4.8.2**      *Monitoring Schedule for Next Month*

The tentative schedule of TSP and noise monitoring for the next reporting period is presented in *Annex D3*. Environmental monitoring will be conducted at the same monitoring locations in the reporting period.

#### **4.8.3**      *Construction Programme for the Next Month*

The most up-to-date construction programme for the Project is presented in *Annex D8*.

## 5 CENTRAL DROP SHAFT

### 5.1 CONSTRUCTION ACTIVITIES DURING THE REPORTING MONTH

A summary of the major construction activities undertaken in this reporting period is shown in *Table 5.1*. The location of the construction activities is shown in *Annex E1*.

*Table 5.1 Summary of Construction Activities Undertaken from 1 to 30 September 2012 at Central Drop Shaft*

Construction Activities Undertaken
• General site clean work.

### 5.2 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project since December 2009 is presented in *Table 5.2* below.

*Table 5.2 Summary of Environmental Licensing, Notification and Permit Status at Central Drop Shaft*

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Wastewater Discharge License	Central PTW Drop Shaft WT0005131-2009	09 October 2009 -31 October 2014	--
Chemical Waste Producer Registration	Central PTW Drop Shaft 5213-115-G2347-06	--	--
Construction Noise Permit CNP	Central Drop Shaft GW-RS0042-11	14 January 2011 – 4 July 2011	Expired. No CNP is required as no works will take place during restricted hours.

### 5.3 ENVIRONMENTAL MONITORING REQUIREMENTS

#### 5.3.1 Air Quality Monitoring

##### *Monitoring Location*

In accordance with the EM&A Manual, 24-hour and 1-hour averaged Total Suspended Particulates (TSP) levels should be conducted at designated monitoring stations. Since access to some of the proposed monitoring locations stated in the EM&A Manual was denied or not available, alternative locations were proposed and agreed by the ER and IEC. The construction air quality monitoring station for this Contract is listed in *Table 5.3* and shown in *Annex E2*.

**Table 5.3 Construction Phase Air Monitoring Location at Central Drop Shaft**

Worksite	Construction Air Quality Monitoring Station			
	ID in EM&A Manual	ID	Location	Remark
Central	-	AM4_2	A Location within the DSD Central PTW	<ul style="list-style-type: none"> <li>• Access to Sheung Wan Fire Station (CM_C1) was rejected.</li> <li>• All possible locations along Connaught Road West and Connaught Road East have been exhausted and no suitable location is identified due to the rejection by the premise owner, security reasons, the absence of guaranteed access or inaccessibility. AM4 was the alternative location.</li> <li>• Since air monitoring station AM4 has to return to DSD for other Work Contract, AM4_2 is an alternative location to replace AM4.</li> </ul>

*Monitoring Parameters, Frequency and Programme*

Air quality monitoring has been conducted in accordance with the requirements stipulated in the EM&A Manual (Table 5.4). The monitoring programme for this reporting period is shown in Annex E3.

**Table 5.4 TSP Monitoring Parameter and Frequency at Central Drop Shaft**

Parameter	Frequency
24-hour average TSP	Once in every 6 days
1-hour average TSP	3 times in every 6 days

*Monitoring Equipment*

Continuous 24-hour and 1-hour averaged TSP monitoring were performed using High Volume Samplers (HVS) with appropriate sampling inlets installed, located at the designated monitoring station. The performance specification of HVS complied with the standard method “Determination of Suspended Particulate Matter in the Atmosphere (High Volume Method)” as stipulated in US EPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50 Appendix B). Table 5.5 summarises the equipment that was deployed for the 24-hour and 1-hour averaged TSP monitoring.

**Table 5.5 TSP Monitoring Equipment at Central Drop Shaft**

Monitoring Station	Monitoring Equipment (HVS and Calibrator)
24-hr and 1-hr TSP	
AM4_2	GMW GS-2310 (S/N 9315), CM-AIR-43 (S/N 0438320)

## *Monitoring Methodology*

### Installation

The setup location of the HVS at monitoring stations was listed in *Table 5.3*. The HVS was free-standing with no obstruction.

The following criteria have been considered in the installation of the HVSs:

- appropriate support to secure the samplers against gusty wind were provided at AM4\_2;
- a minimum of 2 m separation from walls, parapets and penthouses was required for rooftop samplers;
- no furnace or incinerator flues were nearby;
- airflow around the sampler was unrestricted; and
- permission was obtained to set up the samplers and to gain access to the monitoring stations.

### Preparation of Filter Papers

- glass fibre filters were labelled and sufficient filters that were clean and without pinholes were selected;
- all filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than  $\pm 3$  °C; the relative humidity (RH) was 40%; and
- SGS Hong Kong Ltd, a HOKLAS accredited laboratory, implements comprehensive quality assurance and quality control programmes.

### Field Monitoring

- the power supply was checked to ensure that the HVSs were working properly;
- the filter holder and the area surrounding the filter were cleaned;
- the filter holder was removed by loosening the foul bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully;
- the filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter;
- the swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges;



- then the shelter lid was closed and secured with the aluminium strip;
- the HVSs were warmed-up for about 5 minutes to establish run-temperature conditions;
- a new flow rate record sheet was set into the flow recorder;
- the flow rates of the HVSs were checked and adjusted to between 1.22 - 1.37 m<sup>3</sup>min<sup>-1</sup> which were within the range specified in the EM&A Manual (ie 0.6 – 1.7 m<sup>3</sup>min<sup>-1</sup>);
- the programmable timer was set for a sampling period of 24 hours ± 1 hour, and the starting time, weather condition and the filter number were recorded;
- the initial elapsed time was recorded;
- at the end of sampling, the sampled filter was removed carefully and folded in half so that only surfaces with collected particulate matter were in contact;
- the filter paper was then placed in a clean plastic envelope and sealed;
- all monitoring information was recorded on a standard data sheet; and
- filters were sent to SGS Hong Kong Ltd for analysis.

#### Maintenance and Calibration

- the HVSs and their accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply; and
- the flow rate of each HVS with mass flow controller was calibrated using an orifice calibrator. Initial calibrations of the dust monitoring equipment were conducted upon installation and prior to commissioning. Five-point calibration was carried out for HVSs using CM-AIR-43 Calibration Kit. HVSs are calibrated on a bi-monthly basis. The calibration record for the HVS is given in *Annex H*.

#### Wind Data

The nearest weather stations to Central Drop Shaft are located at King's Park and Green Island. Average wind data (wind speed and wind direction) during the monitoring period were obtained from the meteorological stations at Green Island and King's Park of the Hong Kong Observatory (HKO) and are presented in *Annex E5*.

#### *Action and Limit Levels*

The Action and Limit levels have been established and are presented in *Table 5.6*.

**Table 5.6 Action and Limit Levels for Air Quality at Central Drop Shaft**

Parameter	Air Monitoring Station	Action Level, $\mu\text{gm}^{-3}$	Limit Level, $\mu\text{gm}^{-3}$
24-hour average TSP	AM4_2	211	260
1-hour average TSP	AM4_2	393	500

*Event and Action Plan*

The Event and Action Plan (EAP) for air quality monitoring is presented in *Annex I*.

**5.3.2 Noise Monitoring**

*Monitoring Location*

In accordance with the EM&A Manual, monitoring of construction noise impact should be conducted at the designated monitoring stations. Since access to some of the proposed monitoring locations stated in the EM&A Manual was denied or not available, alternative locations was proposed and agreed by the ER and the IEC. The construction noise monitoring locations for this Contract are listed in *Table 5.7* and shown in *Annex E2*.

**Table 5.7 Construction Phase Noise Monitoring Station at Central Drop Shaft**

Worksite	Construction Noise Monitoring Station				
	ID in EM&A Manual	ID	Location	Type of Measurement	Remark
Central	-	NM3	Rooftop of Goldfield Building	Façade	Chi Cheung Building (M4) is not accessible.

*Monitoring Parameters, Frequency and Programme*

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. Additional noise monitoring were also conducted as per required in the EM&A Manual when works were carried out during restricted periods. The monitoring programme for this reporting period is shown in *Annex E3*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ) in decibels dB(A).  $L_{eq(30min)}$  were used as the monitoring parameter for the time period in between 0700 – 1900 hours on normal weekdays, and  $L_{eq(5min)}$  were used as the monitoring parameter for all restricted periods. Supplementary information for data auditing (two statistical sound levels  $L_{10}$  and  $L_{90}$  which are the levels exceeded for 10 and 90 percent of the time respectively) were also recorded during the monitoring for reference. The measured noise levels were logged every 5 minutes throughout the impact monitoring period. *Monitoring Equipment and Methodology*

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures of Technical Memorandum on Noise from*

Construction Work other than Percussive Piling (GW-TM) issued under the Noise Control Ordinance (NCO) (Cap.400).

The sound level meters and calibrator used for the noise measurement, as listed in Table 5.8, comply with IEC 651: 1979 and 804:1985 (Type 1) specification. The calibration certificates of the sound level meters are included in Annex H.

**Table 5.8 Noise Monitoring Equipment at Central Drop Shaft**

Monitoring Station	Monitoring Equipment (Sound Level Meter and Calibrator)
NM3	<ul style="list-style-type: none"> <li>• Calibrator: RION - NC73 (S/N 10997142)</li> <li>• Sound Level Meters: Rion NL-52 (S/N 00710259) and Rion NL-31 (S/N 00603867)</li> </ul>

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

#### *Action and Limit Levels*

The limit levels for the noise monitoring during different monitoring periods are summarised in Table 5.9.

**Table 5.9 Action and Limit Levels for Noise Monitoring at Central Drop Shaft**

Noise Monitoring Location	Measurement Parameters	Limit Level (dB(A))	Remark
NM3	L <sub>eq</sub> (30mins)	75	Normal working hours during weekdays
	L <sub>eq</sub> (5mins)	70	Evening (1900-2300); and Sundays and public holidays (0700-2300)
	L <sub>eq</sub> (5mins)	55	Night-time (2300-0700)

#### *Event and Action Plan*

The Event and Action Plan (EAP) for noise monitoring is presented in Annex I.

### **5.3.3 Cultural Heritage**

No vibration monitoring is required for this reporting month as no blasting of tunnel / shaft works was carried out.

### **5.3.4 Landscape and Visual Monitoring**

In accordance with the EM&A Manual, landscape and visual monitoring is required to ensure that the design, implementation and maintenance of landscape and visual mitigation measures are fully achieved. The landscape and visual monitoring was carried out on site within the environmental site inspection. The monitoring procedures and criteria as described in the EM&A Manual were adopted.

## *Event and Action Plan*

The Event and Action Plan (EAP) for landscape and visual monitoring is presented in *Annex I*.

### **5.4 IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS**

The Contractor has implemented environmental mitigation measures and fulfilled requirements as stated in the EIA Report, Environmental Permit and EM&A Manual. The implementation status during the reporting period is summarised in *Annex E4*.

### **5.5 MONITORING RESULTS**

#### **5.5.1 Air Quality**

A total of 6 sets of 24-hour averaged and 18 sets of 1-hour averaged TSP measurements have been carried out at AM4\_2 during the reporting period. The monitoring data for 24-hour and 1-hour average TSP together with wind data and graphical presentations are presented in *Annex E5*.

The weather condition during the monitoring period varied from sunny to cloudy. The local impacts near the monitoring stations of AM4\_2 were mainly associated with vehicle emissions.

No exceedance of Action and Limit Levels of 1-hr and 24-hr TSP was recorded during the reporting period.

#### **5.5.2 Noise**

A total of 4 sets of 30-minute construction noise measurements were carried out at the monitoring station NM3 during normal weekdays of the reporting period. The monitoring results together with graphical presentations are presented in *Annex E6*. The local impacts observed near the monitoring stations of NM3 were due to traffic noise from Connaught Road Central.

No exceedance of Action and Limit Levels of construction noise was recorded during the reporting period.

#### **5.5.3 Landscape and Visual**

Implementation and maintenance of landscape and visual mitigation measures are fully achieved and no major findings was made during the reporting month.

#### **5.5.4 Cultural Heritage**

No vibration monitoring was conducted for this reporting month as the blasting of tunnel / shaft works has not started.

### 5.5.5 Waste Management

Waste generated from this Project includes inert construction and demolition (C&D) materials, non-inert C&D materials, and marine deposit. Non-inert C&D materials are made up of general refuse, steel and paper/cardboard packaging materials. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. No marine deposits requiring Type 1, 2, and 3 disposal methods were generated during the reporting month. Reference has been made to the Monthly Summary Waste Flow Table prepared by the Contractor (*Annex J*). The waste statistics provided in this section represents the cumulative quantity of wastes generated from all sites in this Project. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in *Table 5.10*. The inert C&D materials and general refuse generated from the Project were disposed of at Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/Chai Wan Barging Point and SENT Landfill respectively. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

**Table 5.10** Quantities of Waste Generated from the Project for all Sites

Month / Year	Quantity					
	C&D Materials (inert) (a)	C&D Materials (non-inert) (b)	Chemical Waste	Marine Deposit		
				Type 1	Type 2	Type 3
September 2012	13,158.97 tonnes	28.5 tonnes	400 L	0 m3	0 m3	0 tonnes

**Notes:**

- Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil. 7,212.5 tonnes of inert C&D materials were disposed of at the Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/ Chai Wan Barging Point and 5,946.47 tonnes of broken rock have been transferred to SENT Landfill for use.
- Non-inert C&D materials include steel, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Steel materials generated from the project are grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. The non-inert C&D materials other than steel and paper/cardboard packaging were disposed of at SENT Landfill. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

### 5.6 ENVIRONMENTAL SITE INSPECTION

Weekly site inspections were carried out by representatives of the Contractor, Engineer and the ET. Site inspections were conducted on 6, 13 and 20 September 2012. Due to the scheduled SSEMC meeting on 27 September 2012 immediately after the joint inspection, inspection was not arranged for the Central Drop Shaft site on that day. No non-compliance was recorded during the site inspections.

Major findings and recommendations are summarised as follows:

- Nil.

5.7 ENVIRONMENTAL NON-CONFORMANCE

5.7.1 Summary of Monitoring Exceedance

No exceedance of the Action and Limit Levels of 1-hour and 24-hour averaged TSP was recorded at the monitoring station during the reporting period.

No exceedance of the Action and Limit Levels of construction noise was recorded at the monitoring station during the reporting period.

5.7.2 Summary of Environmental Non-Compliance

No non-compliance event was recorded during the reporting period.

5.7.3 Summary of Environmental Complaint

No complaint was received during the reporting period. The cumulative complaint log is shown in *Annex E7*.

5.7.4 Summary of Environmental Summon and Successful Prosecution

No summons was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex E7*.

5.8 FUTURE KEY ISSUES

5.8.1 Key Issues for the Coming Month

Works to be undertaken in the coming two monitoring periods are summarised in *Table 5.11*.

**Table 5.11 Construction Works to be Undertaken in the Coming Two Months at Central Drop Shaft**

---

**Work to be carried out**

- General site clean work.
- 

5.8.2 Monitoring Schedule for Next Month

The tentative schedule of TSP and noise monitoring for the next reporting period is presented in *Annex E3*. Environmental monitoring will be conducted at the same monitoring locations in the reporting period.

5.8.3 Construction Programme for the Next Month

The most up-to-date construction programme for the Project is presented in *Annex E8*.

**6.1 CONSTRUCTION ACTIVITIES DURING THE REPORTING MONTH**

A summary of the major construction activities undertaken in this reporting period is shown in *Table 6.1*. The location of the construction activities is shown in *Annex F1*.

**Table 6.1** *Summary of Construction Activities Undertaken from 1 to 30 September 2012 at the Sai Ying Pun Junction Shaft*

Construction Activities Undertaken
<ul style="list-style-type: none"> <li>• Pit bottom steelwork, bunton, services and FSD ladderway installation; and</li> <li>• Alimak installation.</li> </ul>

**6.2 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS**

A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project since December 2009 is presented in *Table 6.2*.

**Table 6.2** *Summary of Environmental Licensing, Notification and Permit Status at Sai Ying Pun Junction Shaft*

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Wastewater Discharge License	Sai Ying Pun Junction Shaft WT00006884-2010	11 June 2010 - 31 October 2014	--
Chemical Waste Producer Registration	Sai Ying Pun Junction Shaft 5213-112-G2347-05	--	--
Construction Noise Permit CNP	Sai Ying Pun Junction Shaft GW-RS0383-12	5 May 2012 - 4 November 2012	--

**6.3 ENVIRONMENTAL MONITORING REQUIREMENTS****6.3.1 Air Quality Monitoring**

Due to contractual arrangements, air quality monitoring was implemented by the Environmental Team of Contract No. *DC/2007/24 of Harbour Area Treatment Scheme Stage 2A (HATS2A) - Construction of Sewage Conveyance System from Aberdeen to Stonecutters Island*.

*Monitoring Location*

In accordance with the EM&A Manual, 24-hour and 1-hour averaged Total Suspended Particulates (TSP) levels should be conducted at designated monitoring stations. Since access to some of the proposed monitoring locations stated in the EM&A Manual was denied or not available, alternative

locations were proposed and agreed by the ER and IEC. The construction air quality monitoring station for this Contract is listed in *Table 6.3* and shown in *Annex F2*.

**Table 6.3** *Construction Phase Air Monitoring Location at Sai Ying Pun Junction Shaft*

Worksite	Construction Air Quality Monitoring Station			Remark
	ID in EM&A Manual	ID	Location	
Fung Mat Street	CM_FM1	AM5	Western Wholesale Food Market	-

*Monitoring Parameters, Frequency and Programme*

Air quality monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual (*Table 6.4*). The monitoring programme provided by *Contract No. DC/2007/24 – Harbour Area Treatment Scheme Stage 2A (HATS 2A) Construction of Sewage Conveyance System from Aberdeen to Sai Ying Pun* for this reporting period is shown in *Annex F3*.

**Table 6.4** *TSP Monitoring Parameter and Frequency at Sai Ying Pun Junction Shaft*

Parameter	Frequency
24-hour average TSP	Once in every 6 days
1-hour average TSP	3 times in every 6 days

*Wind Data Monitoring*

The nearest weather stations to Sai Ying Pun Junction Shaft are located at King’s Park Station and Green Island. Average wind data (wind speed and wind direction) during the monitoring period were obtained from the meteorological stations at Green Island and King’s Park of the Hong Kong Observatory (HKO) and are presented in *Annex F5*.

*Action and Limit Levels*

The Action and Limit levels have been established and are presented in *Table 6.5*.

**Table 6.5** *Action and Limit Levels for Air Quality at Sai Ying Pun Junction Shaft*

Parameter	Air Monitoring Station	Action Level, $\mu\text{gm}^{-3}$	Limit Level, $\mu\text{gm}^{-3}$
24-hour average TSP	AM5	188	260
1-hour average TSP	AM5	332	500

*Event and Action Plan*

The Event and Action Plan (EAP) for air quality monitoring is presented in *Annex I*.



### 6.3.2 Noise Monitoring

#### Monitoring Location

In accordance with the EM&A Manual, monitoring of construction noise impact should be conducted at the designated monitoring stations. Since access to some of the proposed monitoring locations stated in the EM&A Manual was denied or not available; alternative locations were proposed and agreed by the ER and IEC. The construction noise monitoring location for this Contract is listed in *Table 6.6* and shown in *Annex F2*.

**Table 6.6 Construction Phase Noise Monitoring Station at Sai Ying Pun Junction Shaft**

Worksite	Construction Noise Monitoring Station				
	ID in EM&A Manual	ID	Location	Type of Measurement	Remark
Fung Mat Road	M3	NM4	Rooftop of Block A, Kwan Yick Building Phase III	Façade	-

#### Monitoring Parameters, Frequency and Programme

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. Additional noise monitoring were also conducted as per required in the EM&A Manual when works were carried out during restricted periods. The monitoring programme for this reporting period is shown in *Annex F3*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ) in decibels dB(A).  $L_{eq(30min)}$  were used as the monitoring parameter for the time period in between 0700 – 1900 hours on normal weekdays, and  $L_{eq(5min)}$  were used as the monitoring parameter for all restricted periods. Supplementary information for data auditing (two statistical sound levels  $L_{10}$  and  $L_{90}$  which are the levels exceeded for 10 and 90 percent of the time respectively) were also recorded during the monitoring for reference. The measured noise levels were logged every 5 minutes throughout the impact monitoring period.

#### Monitoring Equipment and Methodology

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures of Technical Memorandum on Noise from Construction Work other than Percussive Piling (GW-TM)* issued under the *Noise Control Ordinance (NCO) (Cap.400)*.

The sound level meters and calibrator used for the noise measurement, as listed in *Table 6.7*, comply with IEC 651: 1979 and 804:1985 (Type 1) specifications. The calibration certificates of the sound level meters are included in *Annex H*.

**Table 6.7** *Noise Monitoring Equipment at Sai Ying Pun Junction Shaft*

Monitoring Station	Monitoring Equipment (Sound Level Meter and Calibrator)
NM4	<ul style="list-style-type: none"> <li>• Calibrator: RION - NC73 (S/N 10997142)</li> <li>• Sound Level Meters: Rion NL-52 (S/N 00710259) and Rion NL-31 (S/N 00603867)</li> </ul>

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

*Action and Limit Levels*

The limit levels for the noise monitoring during different monitoring periods are summarised in *Table 6.8*.

**Table 6.8** *Limit Levels for Noise Monitoring at Sai Ying Pun Junction Shaft*

Noise Monitoring Location	Measurement Parameter	Limit Level (dB(A))	Remark
NM4	L <sub>eq</sub> (30mins)	75	Normal working hours during weekdays
	L <sub>eq</sub> (5mins)	70	Evening (1900-2300); and Sundays and public holidays (0700-2300)
	L <sub>eq</sub> (5mins)	55	Night-time (2300-0700)

*Event and Action Plan*

The Event and Action Plan (EAP) for noise monitoring is presented in *Annex I*.

**6.3.3** *Cultural Heritage*

No vibration monitoring is required for this reporting month as no blasting of tunnel / shaft works was carried out.

**6.3.4** *Landscape and Visual Monitoring*

In accordance with the EM&A Manual, landscape and visual monitoring is required to ensure that the design, implementation and maintenance of landscape and visual mitigation measures are fully achieved. The landscape and visual monitoring was carried out on site within the environmental site inspection. The monitoring procedures and criteria as described in the EM&A Manual were adopted.

*Event and Action Plan*

The Event and Action Plan (EAP) for landscape and visual monitoring is presented in *Annex I*.

## **6.4** *IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS*

The Contractor has implemented environmental mitigation measures and fulfilled requirements as stated in the EIA Report, the Environmental Permit and EM&A Manual. The implementation status during the reporting period is summarised in *Annex F4*.

## **6.5** *MONITORING RESULTS*

### **6.5.1** *Air Quality*

A total of 6 sets of 24-hour averaged and 18 sets of 1-hour averaged TSP measurements were carried out at AM5 during the reporting period. The monitoring data for 24-hour and 1-hour averaged TSP together with wind data and graphical presentations are presented in *Annex F5*.

The weather condition during the monitoring period was sunny. The local impacts near the monitoring stations of AM5 were mainly associated with vehicle emissions.

No exceedance of Action and Limit Levels of 1-hr and 24-hr TSP was recorded during the reporting period.

### **6.5.2** *Noise*

A total of 4 sets of 30-minute construction noise measurements were carried out at the monitoring station NM4 during normal weekdays of the reporting period. No exceedance of limit level for noise monitoring during normal working hours was recorded.

5 sets of 3 x 5-minute construction noise measurements were carried out during restricted hours on 2, 11, 16, 25 and 30 September 2012. No exceedance of limit level for noise monitoring during restricted hours was recorded.

The monitoring results together with graphical presentations are presented in *Annex F6*. The local impacts observed near the monitoring stations of NM4 were due to traffic noise from Connaught Road West.

### **6.5.3** *Landscape and Visual*

Implementation and maintenance of landscape and visual mitigation measures are fully achieved and no major finding was made during the reporting month.

### **6.5.4** *Cultural Heritage*

No vibration monitoring was conducted for this reporting month as the blasting of tunnel / shaft works has not started.

### 6.5.5 Waste Management

Waste generated from this Project includes inert construction and demolition (C&D) materials, non-inert C&D materials, and marine deposit. Non-inert C&D materials are made up of general refuse, steel and paper/cardboard packaging materials. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. No marine deposits requiring Type 1, 2, and 3 disposal methods were generated during the reporting month. Reference has been made to the Monthly Summary Waste Flow Table prepared by the Contractor (*Annex J*). The waste statistics provided in this section represent the cumulative quantity of wastes generated from all sites in this Project. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in *Table 6.9*. The inert C&D materials and general refuse generated from the Project were disposed of at Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/Chai Wan Barging Point and SENT Landfill respectively. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

**Table 6.9** Quantities of Waste Generated from the Project for all Sites

Month / Year	Quantity					
	C&D Materials (inert) (a)	C&D Materials (non-inert) (b)	Chemical Waste	Marine Deposit		
				Type 1	Type 2	Type 3
September 2012	13,158.97 tonnes	28.5 tonnes	400 L	0 m3	0 m3	0 tonnes

**Notes:**

- Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil. 7,212.5 tonnes of inert C&D materials were disposed of at the Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/ Chai Wan Barging Point and 5,946.47 tonnes of broken rock have been transferred to SENT Landfill for use.
- Non-inert C&D materials include steel, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Steel materials generated from the project are grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. The non-inert C&D materials other than steel and paper/cardboard packaging were disposed of at SENT Landfill. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

### 6.6 ENVIRONMENTAL SITE INSPECTION

Joint site inspections were conducted by representatives of the Contractor, Engineer and the ET on 6, 13 and 20 September 2012. Due to the scheduled SSEMC meeting on 27 September 2012 immediately after the joint inspection, inspection was not arranged for the Wan Chai site on that day. No non-compliance was recorded during the site inspections.

Major findings observed during the reporting period were summarised as follows:

- Nil.

6.7 ENVIRONMENTAL NON-CONFORMANCE

6.7.1 Summary of Monitoring Exceedance

No exceedance of the Action and Limit Levels of 1-hour and 24-hour averaged TSP was recorded at the monitoring station during the reporting period.

No exceedance of the Noise Limit Levels was recorded at the monitoring station during both normal working hours and restricted hours in the reporting period.

6.7.2 Summary of Environmental Non-Compliance

No non-compliance event was recorded during the reporting period.

6.7.3 Summary of Environmental Complaint

No complaint was received during the reporting period. The cumulative complaint log is shown in Annex F7.

6.7.4 Summary of Environmental Summon and Successful Prosecution

No summons was received during the reporting period. The cumulative summons/prosecution log is shown in Annex F7.

6.8 FUTURE KEY ISSUES

6.8.1 Key Issues for the Coming Month

Works to be undertaken for the coming two monitoring periods are summarised in Table 6.10.

Table 6.10 Construction Works to be Undertaken in the Coming Two Months at Sai Ying Pun Junction Shaft

---

**Work to be taken**

---

- Installation of Shaft & Tunnel Services; and
  - Rail track installation.
- 

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoffs and waste management.

6.8.2 Monitoring Schedule for Next Month

The tentative schedule of TSP and noise monitoring for the next reporting period is presented in Annex F3. Environmental monitoring will be conducted at the same monitoring locations in the reporting period.

6.8.3 Construction Programme for the Next Month

The most up-to-date construction programme for the Project is presented in Annex F8.

## 7 STONECUTTERS ISLAND PRODUCTION AND RISER SHAFTS

### 7.1 CONSTRUCTION ACTIVITIES DURING THE REPORTING MONTH

A summary of the major construction activities undertaken in this reporting period is shown in *Table 7.1*. The locations of the construction activities are shown in *Annex G1*.

**Table 7.1** *Summary of Construction Activities Undertaken from 1 to 30 September 2012 at the Stonecutters Island Production and Riser Shafts*

Construction Activities Undertaken	
<i>Riser Shaft</i>	
<ul style="list-style-type: none"> <li>• Pre-excavation grouting;</li> </ul>	
<i>Production Shaft</i>	
<ul style="list-style-type: none"> <li>• Shaft steel work installation; and</li> <li>• Alimak installation.</li> </ul>	

### 7.2 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project since December 2009 is presented in *Table 7.2*.

**Table 7.2** *Summary of Environmental Licensing, Notification and Permit Status at Stonecutters Island Production and Riser Shafts*

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Wastewater Discharge License	Stonecutters Island Production Shaft and Riser Shaft WT00005069-2009	11 August 2010 - 31 October 2014	--
Chemical Waste Producer Registration	Stonecutters Island Production Shaft and Riser Shaft 5213-269-G2449-07	--	--
Construction Noise Permit CNP	Stonecutters Island Production and Riser Shaft GW-RW0523-12	4 July 2012 – 28 December 2012	

### 7.3 ENVIRONMENTAL MONITORING REQUIREMENTS

#### 7.3.1 Air Quality Monitoring

##### *Monitoring Location*

In accordance with the EM&A Manual, 24-hour and 1-hour averaged Total Suspended Particulates (TSP) levels should be conducted at designated monitoring stations. Since access to some of the proposed monitoring locations stated in the EM&A Manual was denied or not available, alternative locations were proposed and agreed by the ER and IEC. The construction air

quality monitoring station for this Contract is listed in *Table 7.3* and shown in *Annex G2*.

**Table 7.3** *Construction Phase Air Monitoring Location at Stonecutters Island Production and Riser Shafts*

Worksite	Construction Air Quality Monitoring Station			
	ID in EM&A Manual	ID	Location	Remark
SCISTW	-	AM6	Works Site Boundary	<ul style="list-style-type: none"> <li>• Power Access supply for operation of HVS to the rooftop of Government Dockyard Offices (CM_SCI1) was not feasible.</li> <li>• For COSCO HIT Terminal (CM_SCI2), access application was verbally rejected.</li> <li>• Club House (CM_SCI3) is blocked by a high building, which will affect the dust levels during measurement.</li> <li>• Work Site Boundary (near Ngong Shuen Chau Barracks Group 2 (CM_SCI4) was designed for the HATS2A Disinfection Facilities works and the station is separated by a small hill.</li> <li>• Baseline dust monitoring data measured under HATS2A – Provision of Disinfection Facilities at SCISTW will also be obtained for the establishment of the action level for the impact monitoring.</li> </ul>

*Monitoring Parameters, Frequency and Programme*

Air quality monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual (*Table 7.4*). The monitoring programme for this reporting period is shown in *Annex G3*.

**Table 7.4** *TSP Monitoring Parameter and Frequency at Stonecutters Island Production and Riser Shafts*

Parameter	Frequency
24-hour averaged TSP	Once in every 6 days
1-hour averaged TSP	3 times in every 6 days

*Monitoring Equipment*

Continuous 24-hour and 1-hour averaged TSP monitoring were performed using High Volume Samplers (HVS) with appropriate sampling inlets installed, located at the designated monitoring station. The performance specification of HVS complied with the standard method “*Determination of Suspended Particulate Matter in the Atmosphere (High Volume Method)*” as stipulated in *US EPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50 Appendix B)*. *Table 7.5* summarises the equipment that was deployed for the 24-hour and 1-hour averaged TSP monitoring.

**Table 7.5 TSP Monitoring Equipment at Stonecutters Island Production and Riser Shafts**

Monitoring Station	Monitoring Equipment (HVS and Calibrator)
24-hr and 1-hr TSP AM6	GMW GS-2310 (S/N 1254), CM-AIR-43 (S/N 0438320)

*Monitoring Methodology*

Installation

The setup location of the HVS at the monitoring station was listed in *Table 7.3*. The HVS was free-standing with no obstruction.

The following criteria were considered in the installation of the HVSs:

- appropriate support to secure the samplers against gusty wind was provided at AM6;
- a minimum of 2 m separation from walls, parapets and penthouses was required for rooftop samplers;
- no furnace or incinerator flues was nearby;
- airflow around the sampler was unrestricted; and
- permission was obtained to set up the samplers and to gain access to the monitoring stations.

Preparation of Filter Papers

- glass fibre filters were labelled and sufficient filters that were clean and without pinholes were selected;
- all filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than  $\pm 3$  °C; the relative humidity (RH) was 40%; and
- SGS Hong Kong Ltd, a HOKLAS accredited laboratory, implements comprehensive quality assurance and quality control programmes.

Field Monitoring

- the power supply was checked to ensure that the HVSs were working properly;
- the filter holder and the area surrounding the filter were cleaned;
- the filter holder was removed by loosening the foul bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully;



- the filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter;
- the swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges;
- then the shelter lid was closed and secured with the aluminium strip;
- the HVSs were warmed-up for about 5 minutes to establish run-temperature conditions;
- a new flowrate record sheet was set into the flow recorder;
- the flow rates of the HVSs were checked and adjusted to between 1.22 - 1.37 m<sup>3</sup>min<sup>-1</sup> which were within the range specified in the EM&A Manual (ie 0.6 – 1.7 m<sup>3</sup>min<sup>-1</sup>);
- the programmable timer was set for a sampling period of 24 hours ± 1 hour, and the starting time, weather condition and the filter number were recorded;
- the initial elapsed time was recorded;
- at the end of sampling, the sampled filter was removed carefully and folder in half so that only surfaces with collected particulate matter were in contact;
- the filter paper was then placed in a clean plastic envelope and sealed;
- all monitoring information was recorded on a standard data sheet; and
- filters were sent to SGS Hong Kong Ltd for analysis.

#### Maintenance and Calibration

- the HVSs and their accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply; and
- the flow rate of each HVS with mass flow controller were calibrated using an orifice calibrator. Initial calibrations of the dust monitoring equipments were conducted upon installation and prior to commissioning. Five-point calibration was carried out for HVSs using CM-AIR-43 Calibration Kit. HVSs are calibrated on a bi-monthly basis. The calibration record for the HVS is given in *Annex H*.

## Wind Data

The nearest weather station to Stonecutters Island Production and Riser Shafts is located at Tsing Yi. Average wind data (wind speed and wind direction) during the monitoring period were obtained from the meteorological station at Tsing Yi of the Hong Kong Observatory (HKO) and are presented in *Annex G5*.

### *Action and Limit Levels*

The Action and Limit levels have been established and are presented in *Table 7.6*. The baseline air monitoring data (24-hr and 1-hr TSP average) measured under *HATS2A – Provision of Disinfection Facilities at SCISTW (DF)* are also included to establish the Action Level at AM6.

**Table 7.6** *Action and Limit Levels for Air Quality at Stonecutters Island Production and Riser Shafts*

Parameter	Air Monitoring Station	Action Level, $\mu\text{gm}^{-3}$	Limit Level, $\mu\text{gm}^{-3}$
24-hour average TSP	AM6 (with 24-hr TSP data from DF project)	196	260
1-hour average TSP	AM6 (with 1-hr TSP data from DF project)	346	500

### *Event and Action Plan*

The Event and Action Plan (EAP) for air quality monitoring is presented in *Annex I*.

## **7.3.2** *Noise Monitoring*

### *Monitoring Location*

In accordance with the EM&A Manual, monitoring of construction noise impact should be conducted at the designated monitoring stations. Since access to some of the proposed monitoring locations stated in the EM&A Manual were denied or not available, alternative locations were proposed and agreed by the ER and IEC. The construction noise monitoring location for this Contract is listed in *Table 7.7* and shown in *Annex G2*.

**Table 7.7 Construction Phase Noise Monitoring Station at Stonecutters Island Production and Riser Shafts**

Worksite	Construction Noise Monitoring Station				
	ID in EM&A Manual	ID	Location	Type of Measurement	Remark
SCISTW	-	NM5	A Location near the FSD Diving Rescue and Diving Training Centre near the Site Boundary	Free-Field (3dB(A) was added to the measured results)	<ul style="list-style-type: none"> <li>Access to FSD Fire Rescue and Diving Training Centre (M11) was rejected.</li> <li>NM5 is located next to the original proposed location.</li> </ul>

*Monitoring Parameters, Frequency and Programme*

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. Additional noise monitoring was also conducted as per required in the EM&A Manual when works were carried out during restricted periods. The monitoring programme for this reporting period is shown in *Annex G3*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ) in decibels dB(A).  $L_{eq(30min)}$  were used as the monitoring parameter for the time period in between 0700 – 1900 hours on normal weekdays, and  $L_{eq(5min)}$  were used as the monitoring parameter for all restricted periods. Supplementary information for data auditing, two statistical sound levels ( $L_{10}$  and  $L_{90}$  which are the levels exceeded for 10 and 90 percent of the time respectively) were also recorded during the monitoring for reference. The measured noise levels were logged every 5 minutes throughout the impact monitoring period.

*Monitoring Equipment and Methodology*

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures of Technical Memorandum on Noise from Construction Work other than Percussive Piling (GW-TM)* issued under the *Noise Control Ordinance (NCO) (Cap.400)*.

The sound level meters and calibrator used for the noise measurement, as listed in *Table 7.8*, comply with IEC 651: 1979 and 804:1985 (Type 1) specification. The calibration certificates of the sound level meters are included in *Annex H*.

**Table 7.8** *Noise Monitoring Equipment at Stonecutters Island Production and Riser Shafts*

Monitoring Station	Monitoring Equipment (Sound Level Meter and Calibrator)
NM5	<ul style="list-style-type: none"> <li>• Calibrator: Rion NC-73 (S/N 10997142)</li> <li>• Sound Level Meters: Rion NL-31 (S/N 00410224) and Rion NL-31 (S/N 00603867)</li> </ul>

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

A correction of +3 dB(A) was made to the free field measurement at NM5.

*Action and Limit Levels*

The limit levels for the noise monitoring during different monitoring periods are summarised in *Table 7.9*.

**Table 7.9** *Limit Levels for Noise Monitoring at Stonecutters Island Production and Riser Shaft*

Noise Monitoring Location	Measurement Parameter	Limit Level (dB(A))	Remark
NM5	L <sub>eq</sub> (30mins)	75	Normal working hours during weekdays
	L <sub>eq</sub> (5mins)	70	Evening (1900-2300); and Sundays and public holidays (0700-2300)
	L <sub>eq</sub> (5mins)	55	Night-time (2300-0700)

*Event and Action Plan*

The Event and Action Plan (EAP) for noise monitoring is presented in *Annex I*.

**7.3.3** *Cultural Heritage*

No vibration monitoring is required for this reporting month as no blasting of tunnel / shaft works was carried out.

**7.3.4** *Landscape and Visual Monitoring*

In accordance with the EM&A Manual, landscape and visual monitoring is required to ensure that the design, implementation and maintenance of landscape and visual mitigation measures are fully achieved. The landscape and visual monitoring was carried out on site within the environmental site inspection. The monitoring procedures and criteria as described in the EM&A Manual were adopted.

## *Event and Action Plan*

The Event and Action Plan (EAP) for landscape and visual monitoring is presented in *Annex I*.

### **7.4 IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS**

The Contractor has implemented environmental mitigation measures and fulfilled the requirements as stated in the EIA Report, Environmental Permit and EM&A Manual. The implementation status during the reporting period is summarised in *Annex G4*.

### **7.5 MONITORING RESULTS**

#### **7.5.1 Air Quality**

A total of 5 sets of 24-hour averaged and 15 sets of 1-hour averaged TSP measurements were carried out at AM6 during the reporting period. The monitoring data for 24-hour and 1-hour averaged TSP together with wind data and graphical presentations are presented in *Annex G5*.

The weather condition during the monitoring period varied from sunny to cloudy. The local impacts near the monitoring stations of AM6 were mainly associated with vehicle emissions.

No exceedance of Action and Limit Levels of 1-hr and 24-hr TSP was recorded during the reporting period.

#### **7.5.2 Noise**

A total of 4 sets of 30-minute construction noise measurements were carried out at the monitoring station NM5 during normal weekdays of the reporting period. No exceedance of limit level for noise monitoring during normal working hours was recorded.

Construction work was also conducted on public holidays and Sundays in this reporting month. 4 sets of 3 x 5-minute construction noise measurements were carried out during restricted hours on 4, 9, 18 and 23 September 2012 during the reporting month. No exceedance of limit level for noise monitoring during restricted hours was recorded.

The monitoring results together with graphical presentations are presented in *Annex G6*. The local impacts observed near the monitoring stations of NM5 included operations at the Government Dockyard, other construction sites activities and traffic within the SCISTW in the vicinity.

### 7.5.3 *Landscape and Visual*

Implementation and maintenance of landscape and visual mitigation measures are fully achieved and no major finding was made during the reporting month.

### 7.5.4 *Cultural Heritage*

No vibration monitoring was conducted for this reporting month as the blasting of tunnel / shaft works has not started.

### 7.5.5 *Waste Management*

Waste generated from this Project includes inert construction and demolition (C&D) materials, non-inert C&D materials, and marine deposit. Non-inert C&D materials are made up of general refuse, steel and paper/cardboard packaging materials. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. No marine deposits requiring Type 1, 2, and 3 disposal methods was generated during the reporting month. Reference has been made to the Monthly Summary Waste Flow Table prepared by the Contractor (*Annex J*). The waste statistics provided in this section represent the cumulative quantity of wastes generated from all sites in this Project. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in *Table 7.10*. The inert C&D materials and general refuse generated from the Project were disposed of at Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/Chai Wan Barging Point and SENT Landfill respectively. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels generated were sent to recyclers for recycling.

Table 7.10 Quantities of Waste Generated from the Project for all Sites

Month / Year	Quantity					
	C&D Materials (inert) (a)	C&D Materials (non-inert) (b)	Chemical Waste	Marine Deposit		
				Type 1	Type 2	Type 3
September 2012	13,158.97 tonnes	28.5 tonnes	400 L	0 m3	0 m3	0 tonnes

**Notes:**

(a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil. 7,212.5 tonnes of inert C&D materials were disposed of at the Tuen Mun Area 38/Tseung Kwan O Area 137 Fill Bank/ Chai Wan Barging Point and 5,946.47 tonnes of broken rock have been transferred to SENT Landfill for use.

(b) Non-inert C&D materials include steel, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Steel materials generated from the project are grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. The non-inert C&D materials other than steel and paper/cardboard packaging were disposed of at SENT Landfill. No plastic was generated but 172 kg of paper/cardboard packaging and 7 kg of steels were generated and sent to recyclers for recycling.

## 7.6 ENVIRONMENTAL SITE INSPECTION

Weekly site inspections were carried out by representatives of the Contractor, Engineer and the ET. Site inspections were conducted on 6, 13, 20 and 27 September 2012. The representative of the IEC joined the site inspection on 27 September 2012. No non-compliance was recorded during the site inspections.

Major findings and recommendations are summarised as follows:

### *Riser Shaft*

- Nil.

### *Production Shaft*

- On 6 September, stagnant water was observed in the drip tray beside the chemical store. The Contractor was reminded to remove the stagnant water frequently, especially after rainfall events.
- On 6 September, stagnant water was observed in the pit near the chemical enhanced wastewater treatment facility. The Contractor was reminded to pump the water out from the pit, especially after rainfall events.
- On 20 September, stagnant water inside the channel was observed near the chemical enhanced sedimentation facility. The Contractor was reminded to remove the stagnant water to avoid mosquito breeding.
- On 27 September, stagnant water inside the channel was observed near the chemical enhanced sedimentation facility. The Contractor was reminded to remove the stagnant water to avoid mosquito breeding and to ensure water in the channel is free flowing to prevent further accumulation of stagnant water in the future

## 7.7 ENVIRONMENTAL NON-CONFORMANCE

### 7.7.1 *Summary of Monitoring Exceedance*

No exceedance of the Action and Limit Levels of 1-hour and 24-hour averaged TSP was recorded at monitoring station during the reporting period.

No exceedance of the Noise Limit Levels was recorded at monitoring station during both normal working hours and restricted hours in the reporting period.

### 7.7.2 *Summary of Environmental Non-Compliance*

No non-compliance event was recorded during the reporting period.

### 7.7.3 *Summary of Environmental Complaint*

No complaint was received during the reporting period. The cumulative complaint log is shown in *Annex G7*.

**7.7.4 Summary of Environmental Summon and Successful Prosecution**

No summon was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex G7*.

**7.8 FUTURE KEY ISSUES**

**7.8.1 Key Issues for the Coming Month**

Works to be undertaken for the coming two monitoring periods are summarised in *Table 7.11*.

**Table 7.11 Construction Works to be Undertaken in the Coming Two Months at Stonecutters Island Production and Riser Shafts**

<b>Work to be taken</b>
<i>Riser Shaft</i> <ul style="list-style-type: none"><li>• Pre-excavation grouting;</li></ul>
<i>Production Shaft</i> <ul style="list-style-type: none"><li>• Installation of Tunnel Services.</li></ul>

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoffs and waste management.

**7.8.2 Monitoring Schedule for the Next Month**

The tentative schedule of TSP and noise monitoring for the next reporting period is presented in *Annex G3*. Environmental monitoring will be conducted at the same monitoring locations in this reporting period.

**7.8.3 Construction Programme for the Next Month**

The most updated construction programme for the Project is presented in *Annex G8*.



## **CONCLUSIONS**

This Environmental Monitoring and Audit (EM&A) Report presents the EM&A programme undertaken during the period from 1 to 30 September 2012 in accordance with EM&A Manual and the requirement under EP-322/2008/E. The conclusions for the five different sites are summarised below.

### **8.1 NORTH POINT PRODUCTION AND DROP SHAFTS**

No exceedance of Action and Limit Levels of 24-hour and 1-hour averaged TSP was recorded at the air quality monitoring stations during the reporting period.

No exceedance of Limit Levels for construction noise was recorded at the monitoring station during the reporting period.

No non-compliance event was recorded during the reporting period.

No complaint or summons/prosecution was received during the reporting period.

### **8.2 WAN CHAI EAST PRODUCTION AND DROP SHAFTS**

No exceedance of Action and Limit Levels of 24-hour and 1-hour averaged TSP was recorded at the air quality monitoring station during the reporting period.

Exceedance of Limit Levels for construction noise was recorded on 25 and 30 September during the restricted hour at the monitoring station.

No non-compliance event was recorded during the reporting period.

No complaint or summons/prosecution was received during the reporting period.

### **8.3 CENTRAL DROP SHAFT**

No exceedance of Action and Limit Levels of 24-hour and 1-hour averaged TSP was recorded at the air quality monitoring station during the reporting period.

No exceedance of Limit Levels for construction noise was recorded at the monitoring station during the reporting period.

No non-compliance event was recorded during the reporting period.

No complaint or summons/prosecution was received during the reporting period.

**8.4** *SAI YING PUN JUNCTION SHAFT*

No exceedance of Action and Limit Levels of 24-hour and 1-hour averaged TSP was recorded at the air quality monitoring station during the reporting period.

No exceedance of Limit Levels for construction noise was recorded at the monitoring station during the reporting period.

No non-compliance event was recorded during the reporting period.

No complaint or summon/prosecution was received during the reporting period.

**8.5** *STONECUTTERS ISLAND PRODUCTION AND RISER SHAFTS*

No exceedance of Action and Limit Levels of 24-hour and 1-hour averaged TSP was recorded at the air quality monitoring station during the reporting period.

No exceedance of Limit Levels for construction noise was recorded at the monitoring station during the reporting period.

No non-compliance event was recorded during the reporting period.


No complaint or summons/prosecution was received during the reporting period.

**8.6** *OVERALL*

The ET has managed the EM&A programme to monitor the compliance status of various environmental requirements, and verify the proper implementation of necessary mitigation measures.

Annex A


## Locations of Works Areas

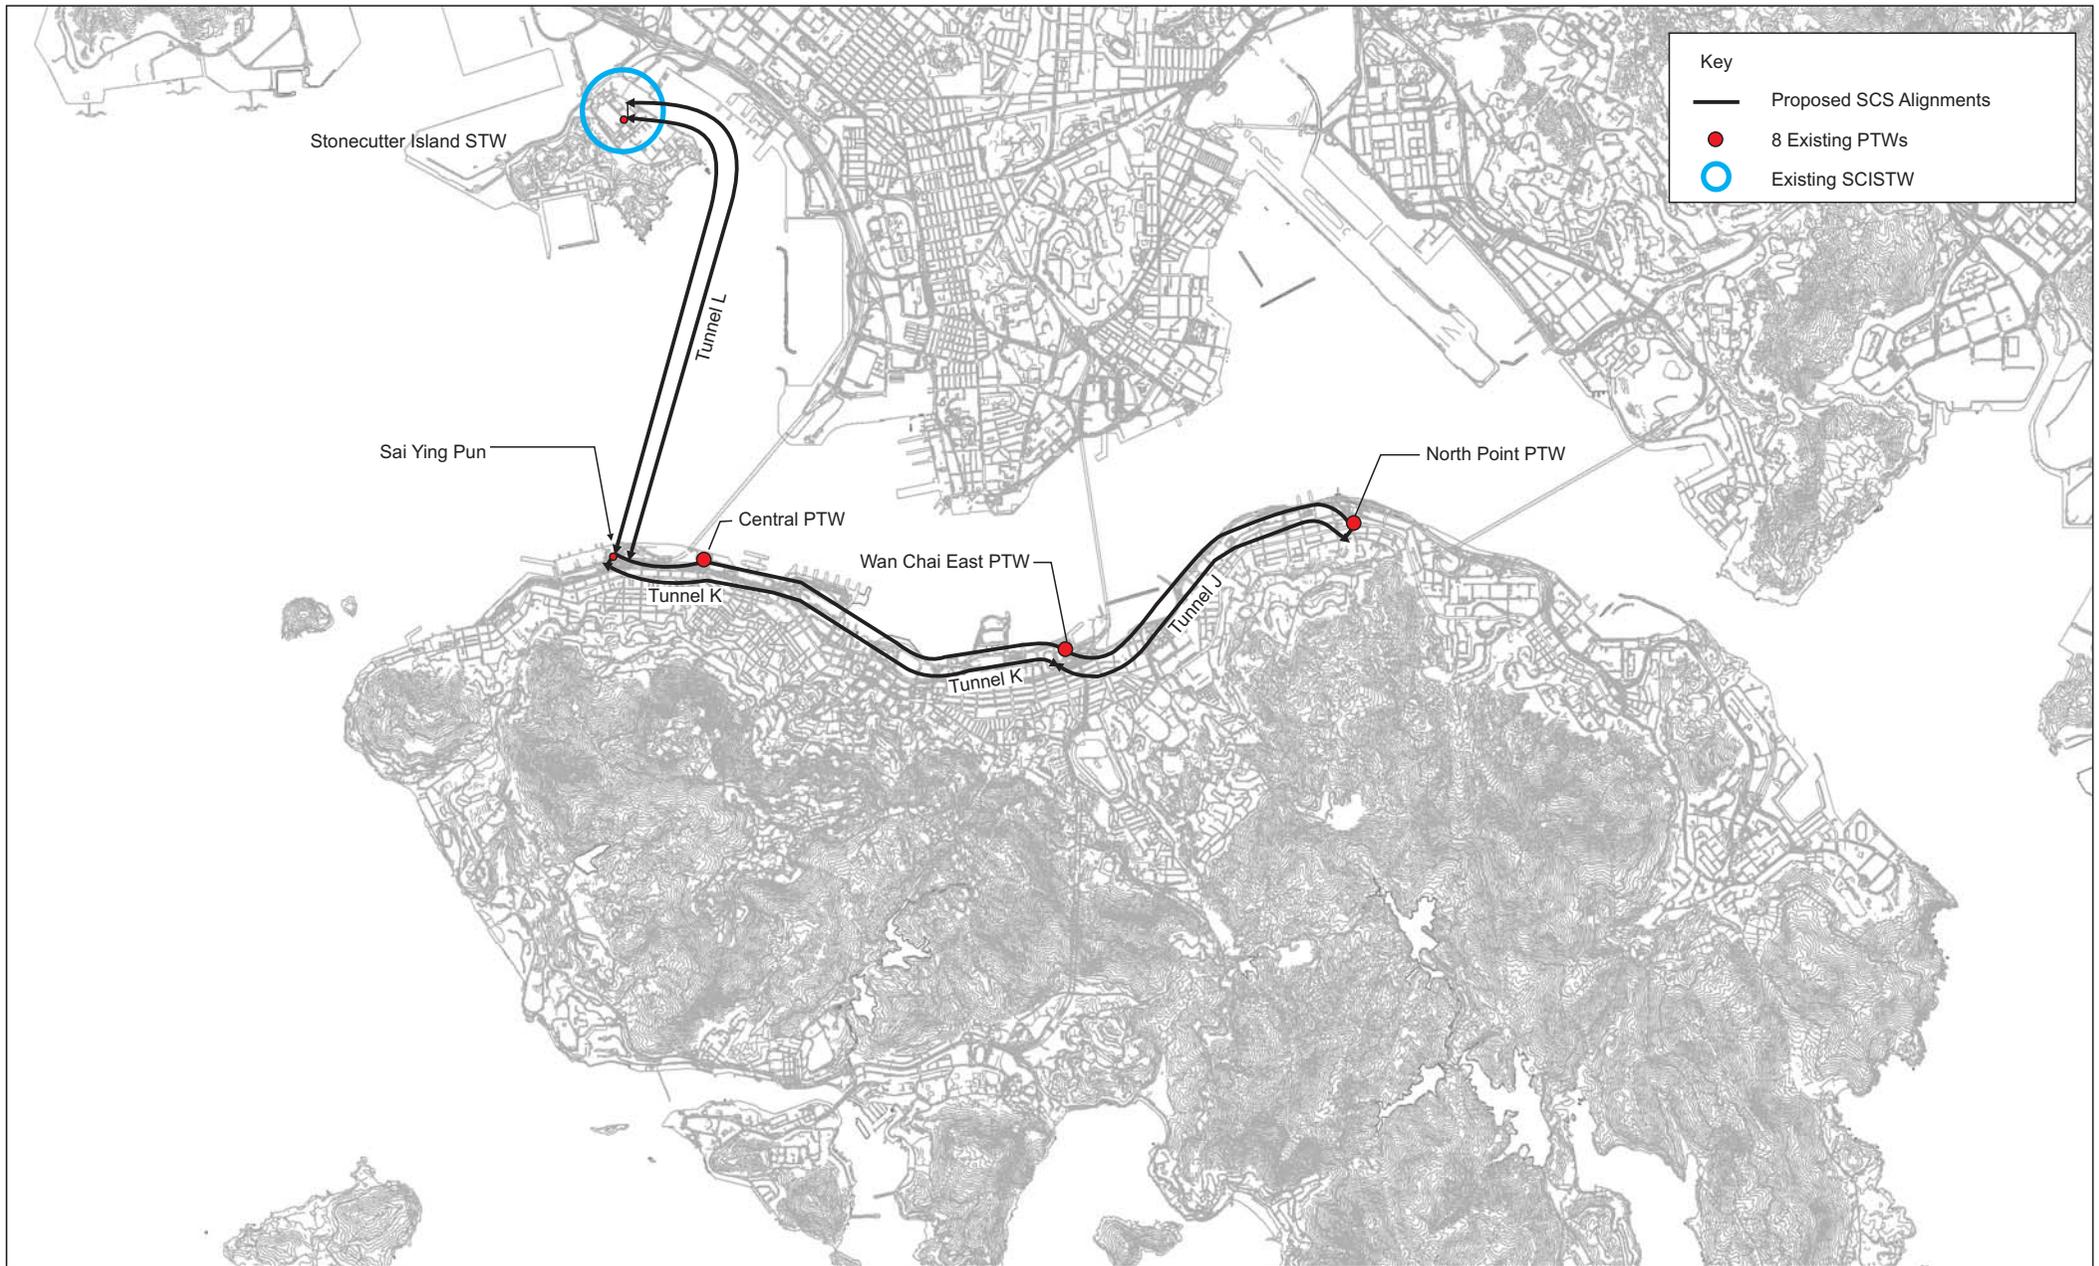

Annex B

## Project Organization Chart and Contact Detail

Project Organization

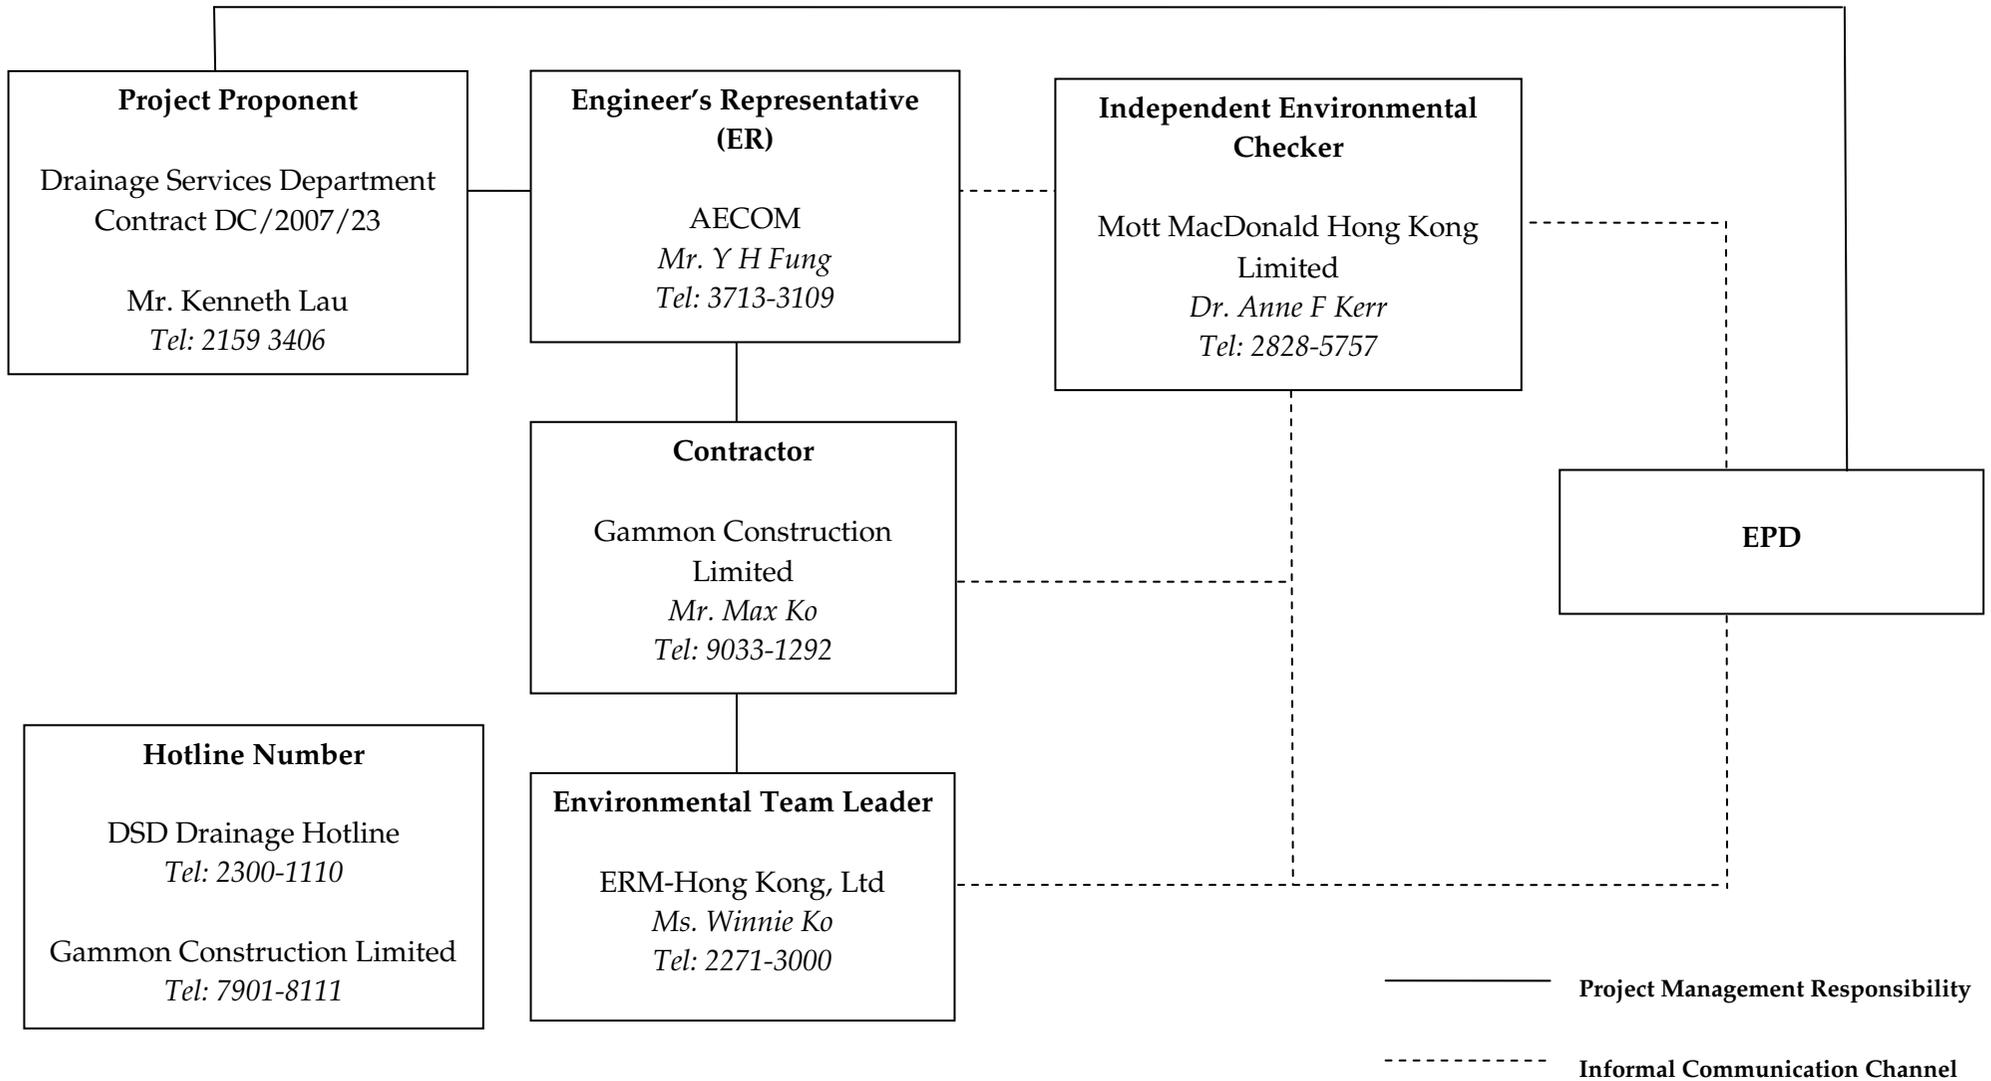


Annex C

## North Point Production and Drop Shafts

**Key**

-  Shaft Excavation Location
-  Site Location

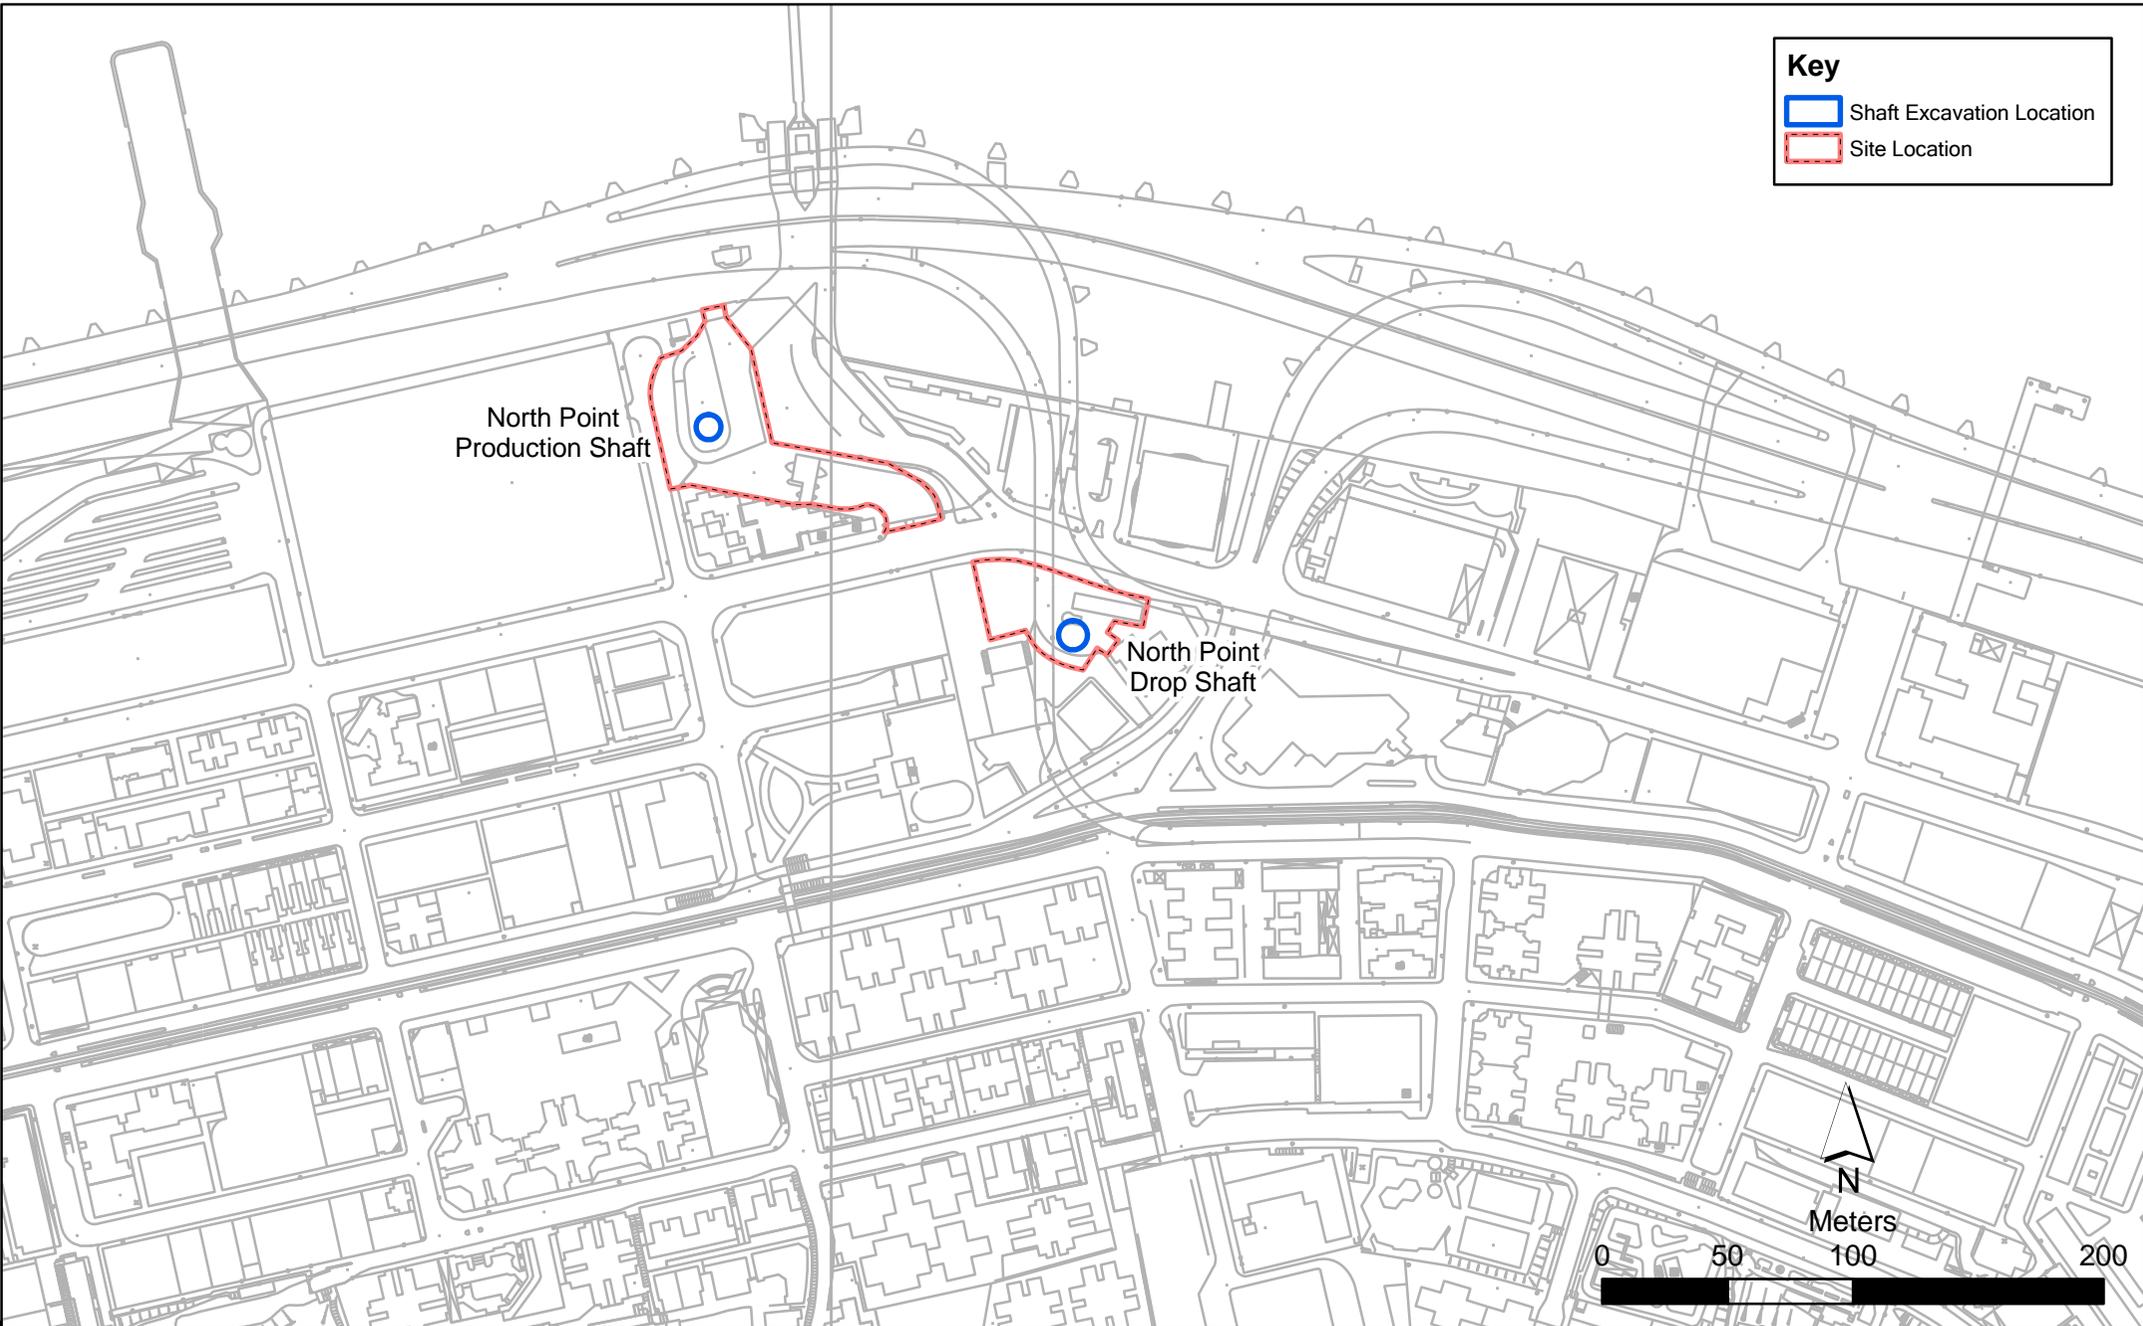

Annex C1


Contract No. DC/2007/23  
 Harbour Area Treatment Scheme Stage 2A  
 Construction of Sewage Conveyance System from North Point to Stonecutters Island  
*Construction Site Locations at North Point*

File: EM&A and proposed station\0104887\_North Point.mxd  
 Date: 29/10/2009

**Environmental  
 Resources  
 Management**





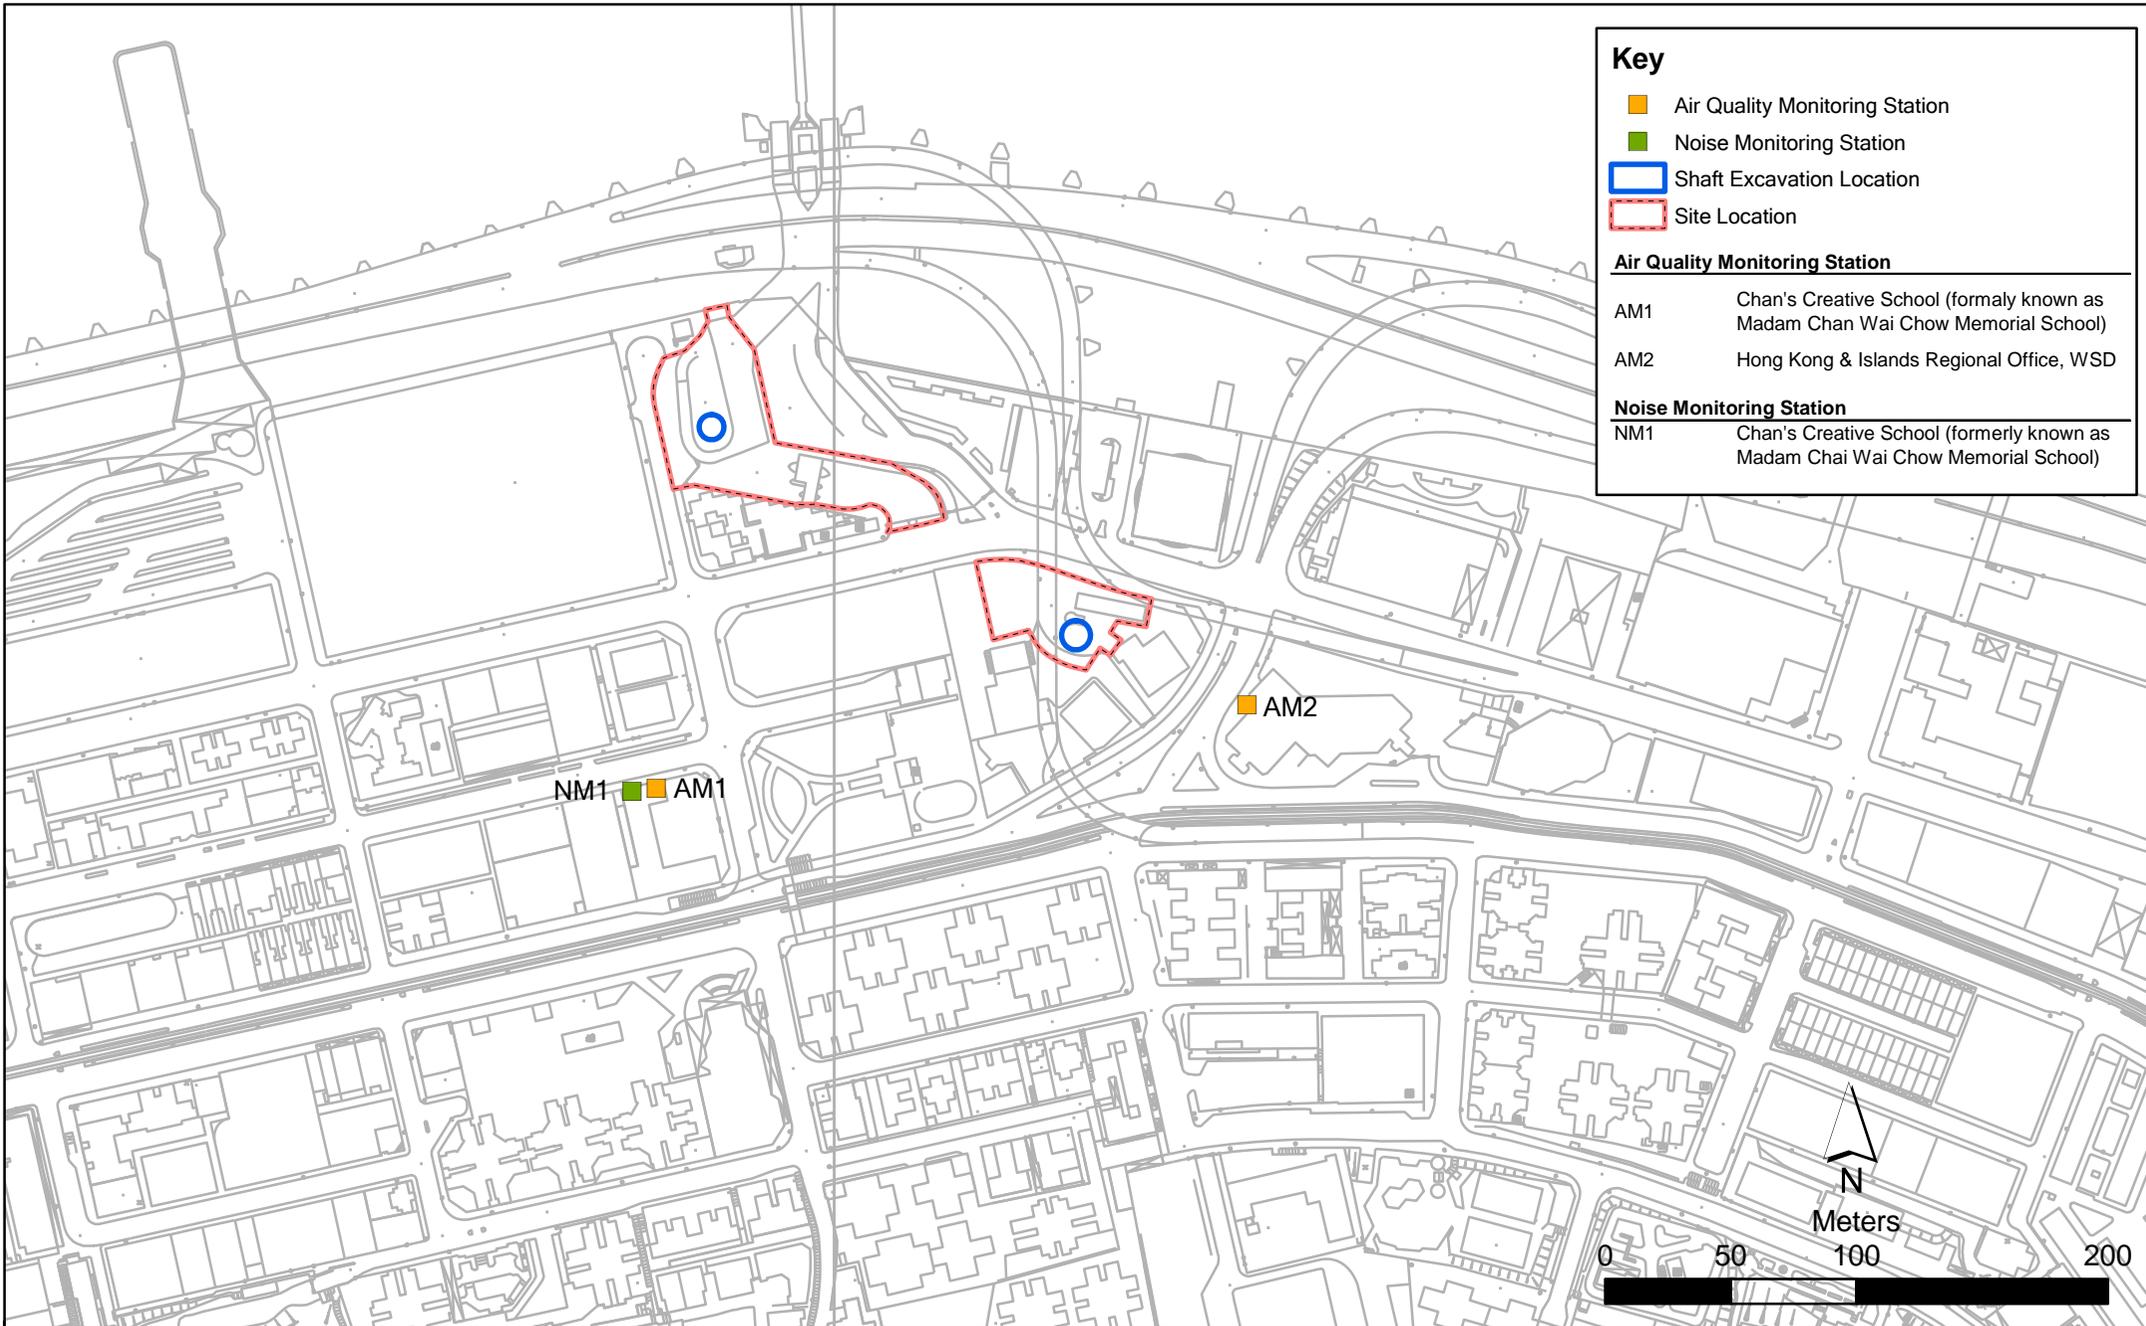

# Annex C3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23  
 Harbour Area Treatment Scheme Stage 2A  
 Construction of Sewage Conveyance System from North Point to Stonecutters Island  
 Impact Construction Air Quality Monitoring Schedule

**AM1 - Chan's Creative School**  
**Monitoring Month : September 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
	1-hr and 24-hr Monitoring					1-hr and 24-hr Monitoring
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
					1-hr and 24-hr Monitoring	
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
				1-hr and 24-hr Monitoring		
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
			1-hr and 24-hr Monitoring			
30-Sep						

**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
	Public Holiday	Public Holiday			1-hr and 24-hr Monitoring	
7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
				1-hr and 24-hr Monitoring		
14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
			1-hr and 24-hr Monitoring			
21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct
	1-hr and 24-hr Monitoring	Public Holiday				1-hr and 24-hr Monitoring
28-Oct	29-Oct	30-Oct	31-Oct			

## Annex C3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23

Harbour Area Treatment Scheme Stage 2A

Construction of Sewage Conveyance System from North Point to Stonecutters Island

Impact Construction Air Quality Monitoring Schedule

AM2 - Hong Kong & Islands Regional Office, WSD

Monitoring Month : September 2012

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
	1-hr and 24-hr Monitoring					1-hr and 24-hr Monitoring
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
					1-hr and 24-hr Monitoring	
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
				1-hr and 24-hr Monitoring		
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
			1-hr and 24-hr Monitoring			
30-Sep						

**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
	Public Holiday	Public Holiday			1-hr and 24-hr Monitoring	
7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
				1-hr and 24-hr Monitoring		
14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
			1-hr and 24-hr Monitoring			
21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct
	1-hr and 24-hr Monitoring	Public Holiday				1-hr and 24-hr Monitoring
28-Oct	29-Oct	30-Oct	31-Oct			

## Annex C3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23

Harbour Area Treatment Scheme Stage 2A

Construction of Sewage Conveyance System from North Point to Stonecutters Island

Impact Construction Noise Quality Monitoring Schedule

NM1 - Chan's Creative School

Monitoring Month : September 2012

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
Noise Monitoring (during daytime of sundays/ public holidays)	Noise Monitoring					
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
		Noise Monitoring (evening time)			Noise Monitoring	
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
Noise Monitoring (during daytime of sundays/ public holidays)				Noise Monitoring		
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
		Noise Monitoring (evening time)	Noise Monitoring			
30-Sep						
Noise Monitoring (during daytime of sundays/ public holidays)						

**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
	Public Holiday	Public Holiday			Noise Monitoring	
7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
		Noise Monitoring (evening time)		Noise Monitoring		
14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
Noise Monitoring (during daytime of sundays/ public holidays)			Noise Monitoring			
21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct
	Noise Monitoring	Noise Monitoring (Evening time) Public Holiday				
28-Oct	29-Oct	30-Oct	31-Oct			
Noise Monitoring (during daytime of sundays/ public holidays)						

**ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Construction Phase</i>	<p>The Air Pollution Control (Construction Dust) Regulation shall be implemented and good site practices shall be incorporated in the contract clauses to minimize construction dust impact. Control measures relevant to this Project are listed below:</p> <ul style="list-style-type: none"> <li>• skip hoist for material transport should be totally enclosed by impervious sheeting;</li> <li>• every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site;</li> <li>• the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;</li> <li>• where a site boundary adjoins a road, streets or other accessible to the public, hoarding of not less than 2.4 m high from ground level should be provided along the entire length except for a site entrance or exit;</li> <li>• every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the 3 sides;</li> <li>• regular watering, with complete coverage, to reduce dust emission from exposed site surfaces and unpaved roads, particularly during dry weather;</li> <li>• site enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines;</li> <li>• open stock piles should be avoided or covered and prevent placing dusty material storage piles near ASRs if possible;</li> <li>• tarpaulin covering of all dusty vehicle loads transported to, from and between site locations; and</li> <li>• instigation of an environmental monitoring auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.</li> </ul>	All work sites / during construction	√



**ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Air Quality	<p>The following watering measures for specific site would be required to control the fugitive dust impacts:</p> <ul style="list-style-type: none"> <li>• watering twice per day within the worksites at North Point PTW; and</li> <li>• watering 8 times per day within worksites at the SCS works area at North Point.</li> </ul>	All work sites / during construction	√
<i>Operational Phase</i>			
Air Quality	<p>Good housekeeping for SCISTW and PTWs listed below should be followed to ameliorate any odour impact from the plant and these standard practices should be included in the plant operator manual.</p> <ul style="list-style-type: none"> <li>• Screens should be cleaned regularly to remove any accumulated organic debris</li> <li>• Grit and screening transfer systems should be flushed regularly with water to remove organic debris and grit</li> <li>• Grit and screened materials should be transferred to closed containers to minimize odour escape</li> <li>• Scum and grease collection wells and troughs should be emptied and flushed regularly to prevent putrefaction of accumulated organics</li> <li>• Skim and remove floating solids and grease from primary clarifiers regularly</li> <li>• Frequent sludge withdrawal from tanks is necessary to prevent the production of gases</li> <li>• Sludge cake should be transferred to closed containers</li> <li>• Sludge containers should be flushed with water regularly</li> </ul>	All work sites / during construction	NA. Measures not required until commencement of operational phase
Air Quality	Commissioning tests for all deodorization system should be included in the Design and Construction Contract Document.	All PTW and SCISTW/ during operational phase	
<i>Construction Phase</i>			
Noise	Use of quiet PME, movable barriers and acoustic mats	All work sites / during construction	√

**ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Noise	<p>Good Site Practice:</p> <ul style="list-style-type: none"> <li>• only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program;</li> <li>• silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program;</li> <li>• mobile plant, if any, should be sited as far from NSRs as possible;</li> <li>• machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;</li> <li>• plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>• material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities;</li> </ul> <p>Environmental audit shall be carried out to ensure that appropriate noise control measures would be properly implemented.</p>	All work sites / during construction	√
<i>Construction Phase</i>			
Water Quality	<p>Construction Site Runoff and General Construction Activities</p> <p>The mitigation measures as outlined in the ProPECC PN 1/94 Construction Site Drainage should be adopted where applicable.</p>	All work sites / during construction	√

**ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Effluent Discharge</p> <p>There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD. Minimum distances of 100 m should be maintained between the discharge points of construction site effluent and the existing saltwater intakes.</p>	All work sites / during construction	√
Water Quality	<p>Accidental Spillage of Chemicals</p> <p>Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.</p>	All work sites / during construction	<>
Water Quality	<p>Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.</p>	All work sites / during construction	<>

*ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE*

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes.</p> <p>General requirements are given as follows:</p> <ul style="list-style-type: none"><li>• Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</li><li>• Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents.</li><li>• Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.</li></ul>	All work sites / during construction	√

**ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	Construction Works in Close Proximity of Storm Drains or Seafront	All work sites / during construction	√
	<p>To minimize the potential water quality impacts from the construction works located at or near any watercourse, the practices outlined below should be adopted where applicable.</p> <ul style="list-style-type: none"> <li>• The use of less or smaller construction plants may be specified to reduce the disturbance to the storm water courses or marine environment.</li> <li>• Temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works.</li> <li>• Stockpiling of construction materials and dusty materials should be covered and located away from any water courses.</li> <li>• Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers.</li> <li>• Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the waterfront, where practicable.</li> <li>• Proper shoring may need to be erected in order to prevent soil/mud from slipping into the storm culvert or sea</li> </ul>		

**ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Operational Phase</i>			
Water Quality	Dual power supply, standby facilities for the main treatment units and standby equipment parts / accessories should be provided as far as possible at the SCISTW to minimize the chance of emergency discharge.	SCISTW and all the Stage 2 PTWs / Operation Stage	NA. Measures not required until commencement of operational phase
Water Quality	Standby unit(s) and dual (backup) power supply would be provided at all the Stage 2 PTWs to reduce the risk of equipment breakdown at the PTWs.	Stage 2 PTWs / Operation Stage	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			
Waste	Reusable steel or concrete panel shutters, fencing and hoarding and signboard should be used as a preferred alternative to items made of wood, to minimise wastage of wood. Attention should be paid to WBTC No. 19/2001 - Metallic Site Hoardings and Signboards to reduce the amount of timber used on construction sites. Metallic alternatives to timber are readily available and should be used rather than new timber. Precast concrete units should be adopted wherever feasible to minimize the use of timber formwork.	All work sites / during the construction period	√
Waste	All waste materials should be segregated into categories covering: <ul style="list-style-type: none"> <li>• excavated materials suitable for reuse on-site;</li> <li>• excavated materials suitable for public filling facilities;</li> <li>• remaining C&amp;D waste for landfill;</li> <li>• chemical waste; and</li> <li>• general refuse for landfill.</li> </ul>	All work sites / during the construction period	√

**ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	<p>Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> <li>• Sort C&amp;D waste from demolition of existing facilities to recover recyclable portions such as metals;</li> <li>• Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>• Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force;</li> <li>• Any unused chemicals or those with remaining functional capacity shall be recycled; and</li> <li>• Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> </ul>	All work sites / during the construction period	√
Waste	<p>Recommendations for good site practices during construction activities include:-</p> <ul style="list-style-type: none"> <li>• Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site</li> <li>• Training of site personnel in proper waste management and chemical waste handling procedures</li> <li>• Develop and provide toolbox talk for on-site sorting of C&amp;D materials to enhance worker’s awareness in handling, sorting, reuse and recycling of C&amp;D materials.</li> <li>• Provision of sufficient waste disposal points and regular collection of waste</li> <li>• Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors</li> </ul>	All work sites / during the construction period	√
Waste	<p>Bentonite slurries used in diaphragm wall construction should be reconditioned and reused wherever practicable. The disposal of residual used bentonite slurry should follow the good practice guidelines stated in ProPECC PN 1/94 “Construction Site Drainage”.</p>	All work sites / during the construction period	√

**ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	Adequate number of portable toilets at temporary works areas or the PTWs to ensure that sewage from site staff would be properly collected.	All work sites / during the construction period	√
Waste	General refuse should be stored in enclosed bins, skips or compaction units separating from C&D material and disposed of at designated landfill.	All work sites / during the construction period	√
Waste	The recyclable component of the municipal waste generated by the workforce, such as aluminium cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.	All work sites / during the construction period	√
Waste	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the approved Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	All work sites / during the construction period	√



**ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	Prior to excavation of the marine deposit layer, the deposit should be tested in accordance with the ETWB TC(W) No. 34/2002 and the results should be presented in a Preliminary Sediment Quality Report. The marine deposit should be disposed of at the disposal site designated by the Marine Fill Committee (MFC) or Director of Environmental Protection (DEP) depending on the test results.	All work sites / during the construction period	√
<i>Construction Phase</i>			
Landscape & Visual	<ul style="list-style-type: none"> <li>• Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.</li> <li>• Existing trees to be retained on site should be carefully protected during construction.</li> <li>• Trees unavoidably affected by the works should be transplanted where practical.</li> <li>• Compensatory tree planting should be provided to compensate for felled trees.</li> <li>• Control of night-time lighting.</li> <li>• Erection of decorative screen hoarding compatible with the surrounding setting.</li> </ul>	All the works areas, PTWs and SCISTW / during the construction period	√
<i>Operational Phase</i>			
Landscape & Visual	<ul style="list-style-type: none"> <li>• Aesthetic design of the façade of PTW and associated structures to harmonize with the surrounding settings.</li> <li>• Shrub and Climbing Plants to soften proposed structures / Roof Greening.</li> <li>• Buffer Tree and Shrub Planting to screen proposed associated structures.</li> <li>• Reinstated of disturbed area</li> </ul>	All the works areas, PTWs and SCISTW / during the construction period	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			

**ANNEX C4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Cultural Heritage	The construction vibration control limit (ppv of 25mm/s) shall be strictly followed.	Identified historical buildings/ structures as mentioned in Tables 15.8 and 15.9. During blasting for tunnel, shafts, effluent conveyance system and disinfection facilities in the vicinity of the buildings/ structures	NA. Vibration monitoring has not been launched during the reporting period.
	Monitoring of vibration limits shall be conducted and reported as a requirement of EM&A programme	Identified historical buildings/ structures as mentioned in Tables 15.8 and 15.9. During blasting for tunnel, shafts, effluent conveyance system and disinfection facilities in the vicinity of the buildings/ structures	NA. Vibration monitoring has not been launched during the reporting period.

Remark:

- √ Compliance of Mitigation Measures
- <> Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- Δ Deficiency of Mitigation Measures but rectified by the Contractor
- NA Not Applicable

## Annex C5 24-hour and 1-hour TSP Monitoring Results

### 1-hour TSP Monitoring Results

#### Station AM1

Date	Start Time	Finish Time	Weather	TSP Concentration (µg/m <sup>3</sup> )	Action Level (µg/m <sup>3</sup> )	Limit Level (µg/m <sup>3</sup> )	Site Conditions / Observations / Remarks	Temperature (°C)	Wind Speed* (m/s)	Sampler ID	Filter ID
3-Sep-12	10:00	11:00	Sunny	175	340	500	Construction work in progress	32.8	<5	1808	5159
	11:02	12:02	Sunny	138	340	500	Construction work in progress	32.8	<5	1808	5161
	12:04	13:04	Sunny	114	340	500	Construction work in progress	32.8	<5	1808	5164
8-Sep-12	9:30	10:30	Sunny	110	340	500	Construction work in progress	31.2	<5	1808	5170
	10:32	11:32	Sunny	114	340	500	Construction work in progress	31.2	<5	1808	5172
	11:34	12:34	Sunny	114	340	500	Construction work in progress	31.2	<5	1808	5173
14-Sep-12	9:45	10:45	Sunny	149	340	500	Construction work in progress	30.5	<5	1808	5180
	10:47	11:47	Sunny	156	340	500	Construction work in progress	30.5	<5	1808	5325
	11:49	12:49	Sunny	153	340	500	Construction work in progress	30.5	<5	1808	5328
20-Sep-12	9:35	10:35	Cloudy	179	340	500	Construction work in progress	29	<5	1808	5350
	10:37	11:37	Cloudy	169	340	500	Construction work in progress	29	<5	1808	5334
	11:39	12:39	Cloudy	159	340	500	Construction work in progress	29	<5	1808	5335
26-Sep-12	10:00	11:00	Cloudy	148	340	500	Construction work in progress	30	<5	1808	5352
	11:02	12:02	Cloudy	161	340	500	Construction work in progress	30	<5	1808	5353
	12:04	13:04	Cloudy	160	340	500	Construction work in progress	30	<5	1808	5357
			<b>Min.</b>	<b>110</b>							
			<b>Max.</b>	<b>179</b>							
			<b>Average</b>	<b>147</b>							

\* Wind Speed data is presented in the Meteorological Data table

## Annex C5 24-hour and 1-hour TSP Monitoring Results

### 1-hour TSP Monitoring Results

#### Station AM2

Date	Start Time	Finish Time	Weather	TSP Concentration (µg/m <sup>3</sup> )	Action Level (µg/m <sup>3</sup> )	Limit Level (µg/m <sup>3</sup> )	Site Conditions / Observations / Remarks	Temperature (°C)	Wind Speed * (m/s)	Sampler ID	Filter ID
3-Sep-12	10:20	11:20	Sunny	161	352	500	Construction work in progress	32.8	<5	0145	5160
	11:22	12:22	Sunny	102	352	500	Construction work in progress	32.8	<5	0145	5160
	12:24	13:24	Sunny	111	352	500	Construction work in progress	32.8	<5	0145	5163
8-Sep-12	9:10	10:10	Sunny	124	352	500	Construction work in progress	31.2	<5	0145	5169
	10:12	11:12	Sunny	107	352	500	Construction work in progress	31.2	<5	0145	5171
	11:14	12:14	Sunny	109	352	500	Construction work in progress	31.2	<5	0145	5174
14-Sep-12	10:00	11:00	Sunny	153	352	500	Construction work in progress	30.5	<5	0145	5179
	11:02	12:02	Sunny	141	352	500	Construction work in progress	30.5	<5	0145	5326
	12:04	13:04	Sunny	148	352	500	Construction work in progress	30.5	<5	0145	5327
20-Sep-12	9:52	10:52	Cloudy	175	352	500	Construction work in progress	29	<5	0145	5349
	10:54	11:54	Cloudy	181	352	500	Construction work in progress	29	<5	0145	5333
	11:56	12:56	Cloudy	156	352	500	Construction work in progress	29	<5	0145	5336
26-Sep-12	9:40	10:40	Cloudy	168	352	500	Construction work in progress	30	<5	0145	5351
	10:42	11:42	Cloudy	161	352	500	Construction work in progress	30	<5	0145	5354
	11:44	12:44	Cloudy	161	352	500	Construction work in progress	30	<5	0145	5356
			<b>Min.</b>	<b>102</b>							
			<b>Max.</b>	<b>181</b>							
			<b>Average</b>	<b>144</b>							

\* Wind Speed data is presented in the Meteorological Data table

## Annex C5 24-hour and 1-hour TSP Monitoring Results

### 24-hour TSP Monitoring Results

#### Station AM1

Start		Finish		Weather	Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m <sup>3</sup> /min)			TSP Conc. (µg/m <sup>3</sup> )	Action Level (µg/m <sup>3</sup> )	Limit Level (µg/m <sup>3</sup> )	Observations / Remarks	Sampler ID	Filter ID
Date	Time	Date	Time		Initial	Final	Initial	Final		Initial	Final	Average						
3-Sep-12	13:45	4-Sep-12	13:45	Sunny	2.7500	2.8910	14757.03	14781.03	24.00	1.20	1.20	1.20	82	185	260	Construction work in progress	1808	5166
8-Sep-12	12:36	9-Sep-12	12:36	Sunny	2.7627	2.9140	14784.03	14808.03	24.00	1.20	1.20	1.20	88	185	260	Construction work in progress	1808	5175
14-Sep-12	12:50	15-Sep-12	12:50	Sunny	2.7755	2.9144	14811.03	14835.03	24.00	1.20	1.20	1.20	80	185	260	Construction work in progress	1808	5329
20-Sep-12	12:42	21-Sep-12	12:42	Cloudy	2.8006	2.9581	14838.03	14862.03	24.00	1.24	1.24	1.24	88	185	260	Construction work in progress	1808	5337
26-Sep-12	13:55	27-Sep-12	13:55	Cloudy	2.7889	2.9411	14865.03	14889.03	24.00	1.24	1.24	1.24	85	185	260	Construction work in progress	1808	5355
													Min.	80				
													Max.	88				
													Average	85				


### 24-hour TSP Monitoring Results

#### Station AM2


Start		Finish		Weather	Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m <sup>3</sup> /min)			TSP Conc. (µg/m <sup>3</sup> )	Action Level (µg/m <sup>3</sup> )	Limit Level (µg/m <sup>3</sup> )	Observations / Remarks	Sampler ID	Filter ID
Date	Time	Date	Time		Initial	Final	Initial	Final		Initial	Final	Average						
3-Sep-12	14:05	4-Sep-12	14:05	Sunny	2.7521	2.8903	15853.93	15877.93	24.00	1.22	1.22	1.22	79	182	260	Construction work in progress	0145	5165
8-Sep-12	12:16	9-Sep-12	12:16	Sunny	2.7598	2.8900	15880.93	15904.93	24.00	1.22	1.22	1.22	74	182	260	Construction work in progress	0145	5176
14-Sep-12	13:06	15-Sep-12	13:06	Sunny	2.7789	2.9112	15907.93	15931.93	24.00	1.22	1.22	1.22	75	182	260	Construction work in progress	0145	5330
20-Sep-12	13:00	21-Sep-12	13:00	Cloudy	2.7911	2.9214	15934.93	15958.93	24.00	1.20	1.20	1.20	75	182	260	Construction work in progress	0145	5338
26-Sep-12	12:46	27-Sep-12	12:46	Cloudy	2.7951	2.9201	15961.93	15985.93	24.00	1.20	1.20	1.20	72	182	260	Construction work in progress	0145	5348
													Min.	72				
													Max.	79				
													Average	75				

### 1-hr TSP Levels AM1 (Chan's Creative School)

— Action Level — Limit Level ◆ AM1

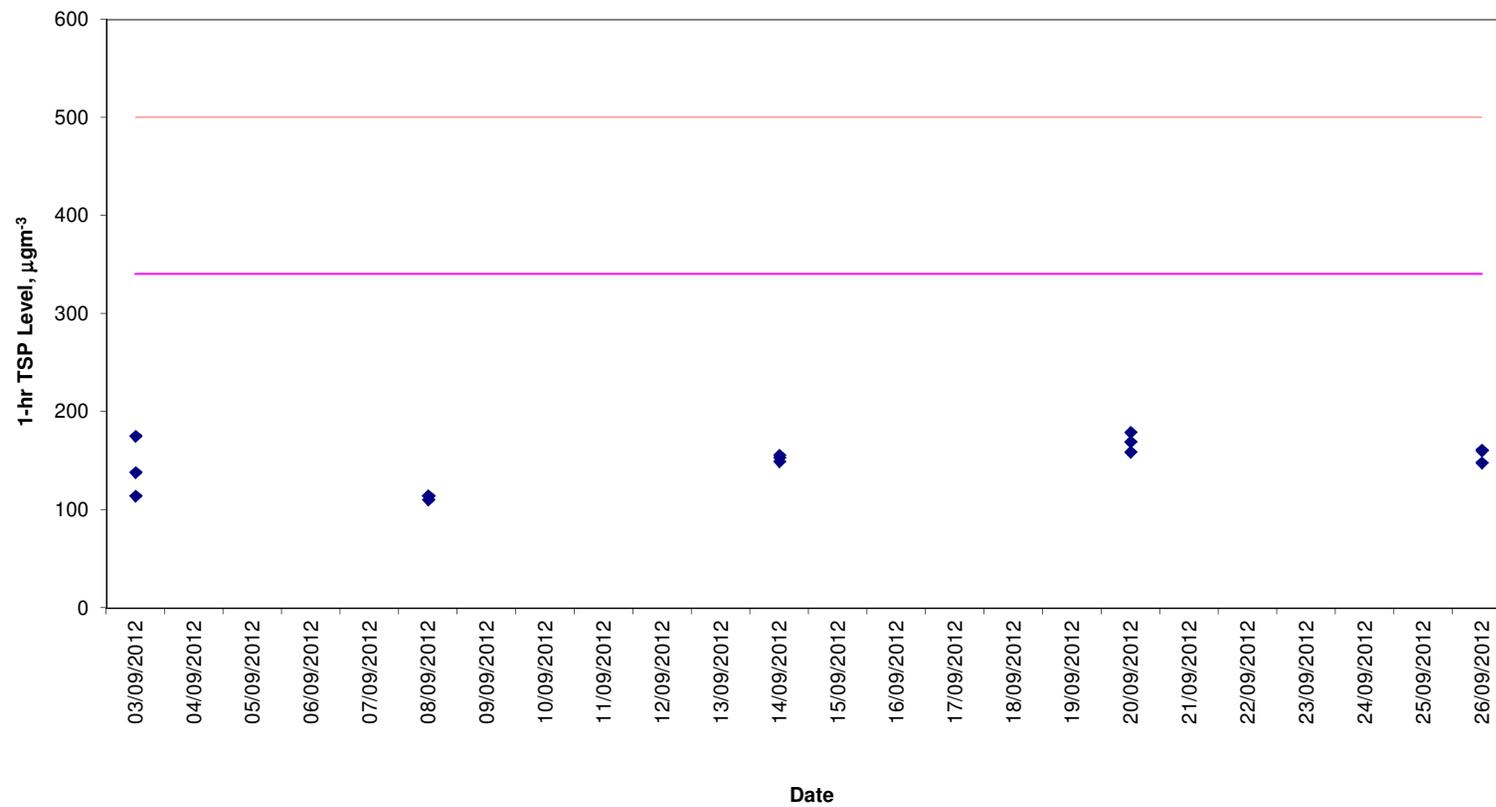


**1-hr TSP Levels**  
**AM2 (Hong Kong & Island Regional Office, WSD)**

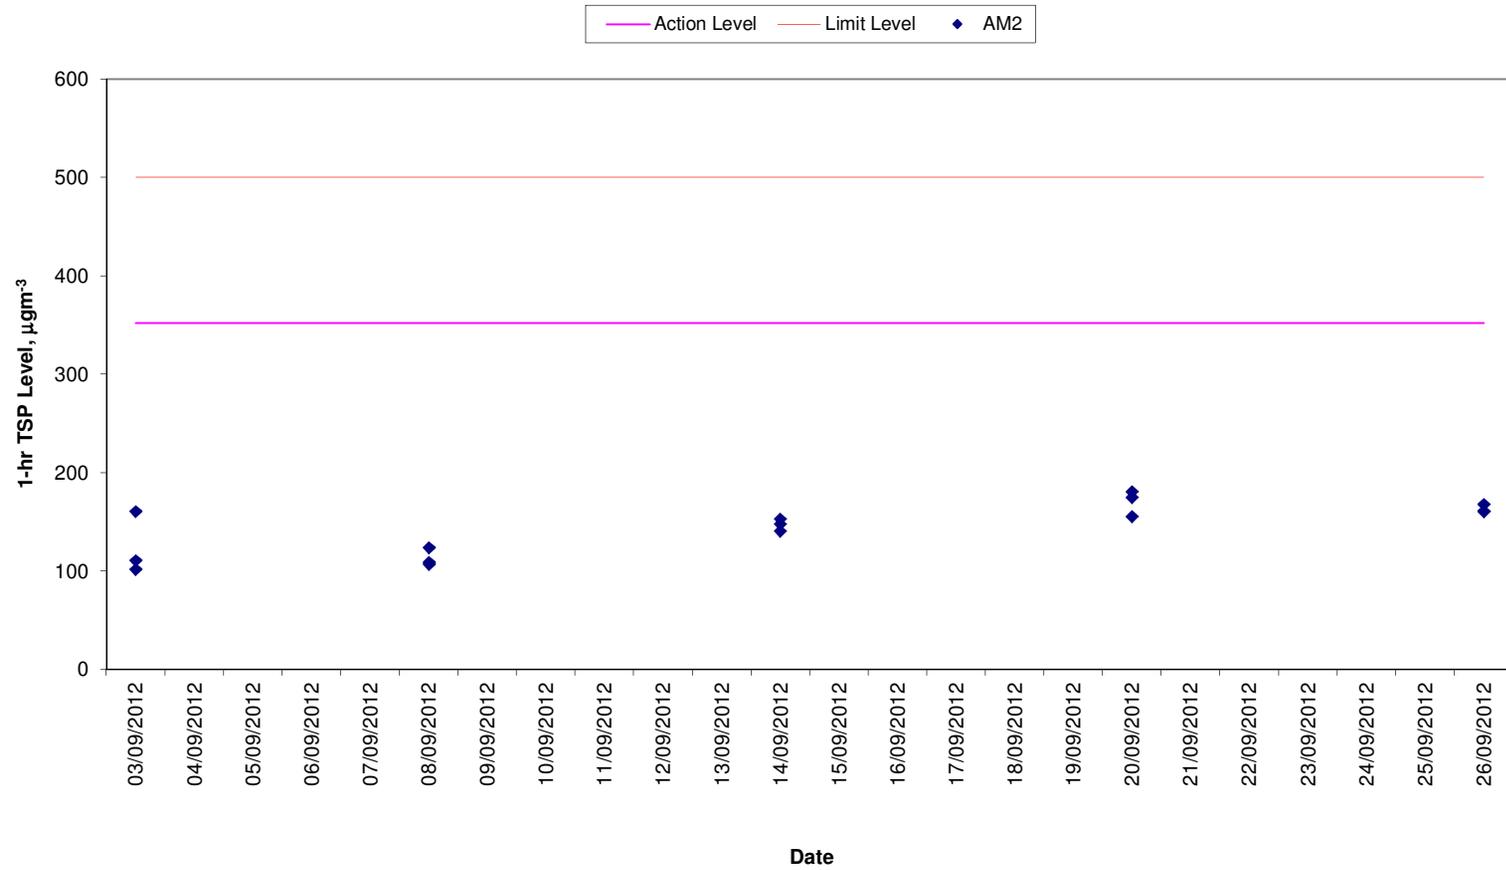

**24-hr TSP Levels  
AM1 (Chan's Creative School)**


AM1    Action Level    Limit Level

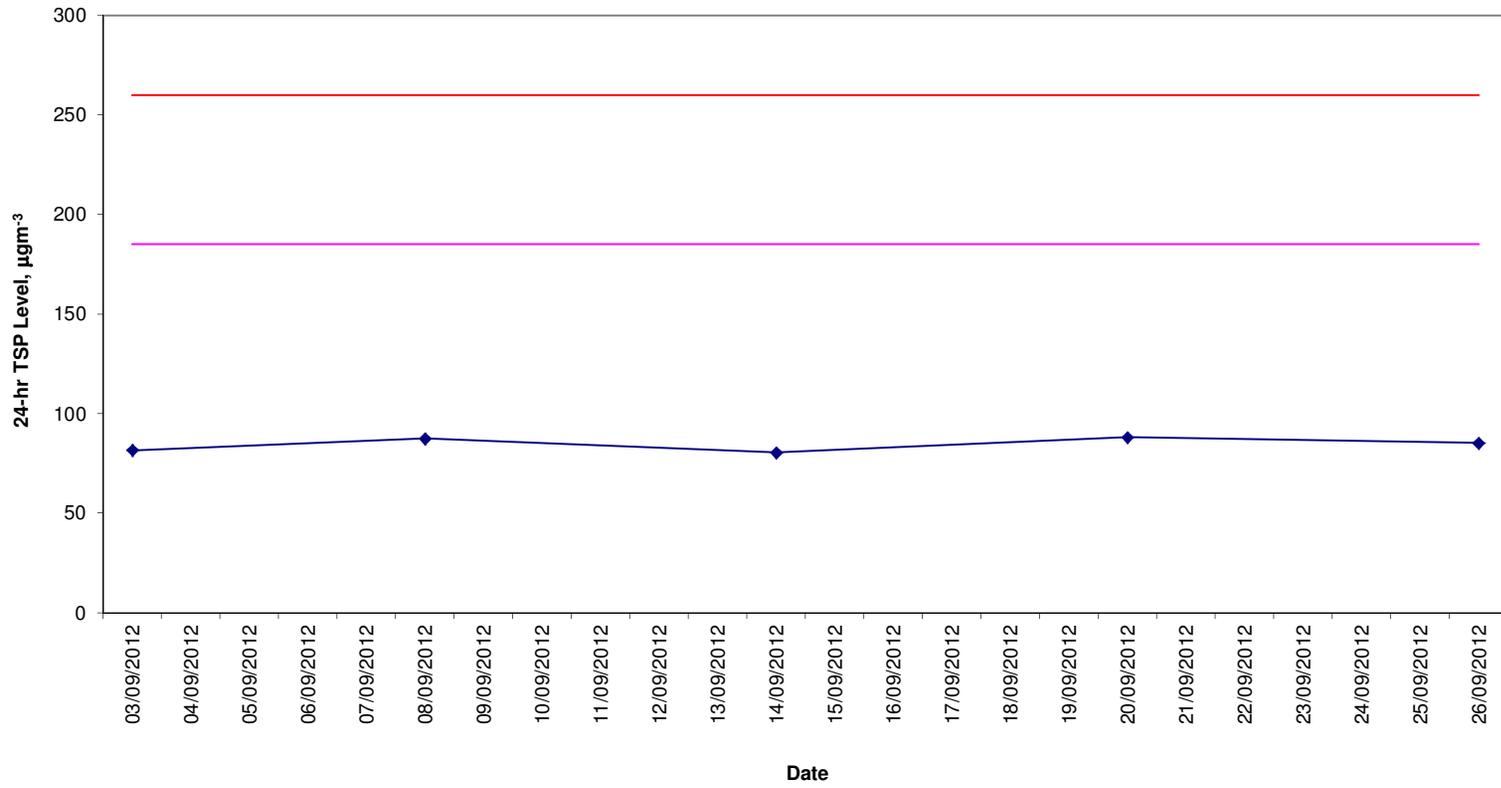



**24-hr TSP Levels**  
**AM2 (Hong Kong & Island Regional Office, WSD)**

AM2    Action Level    Limit Level

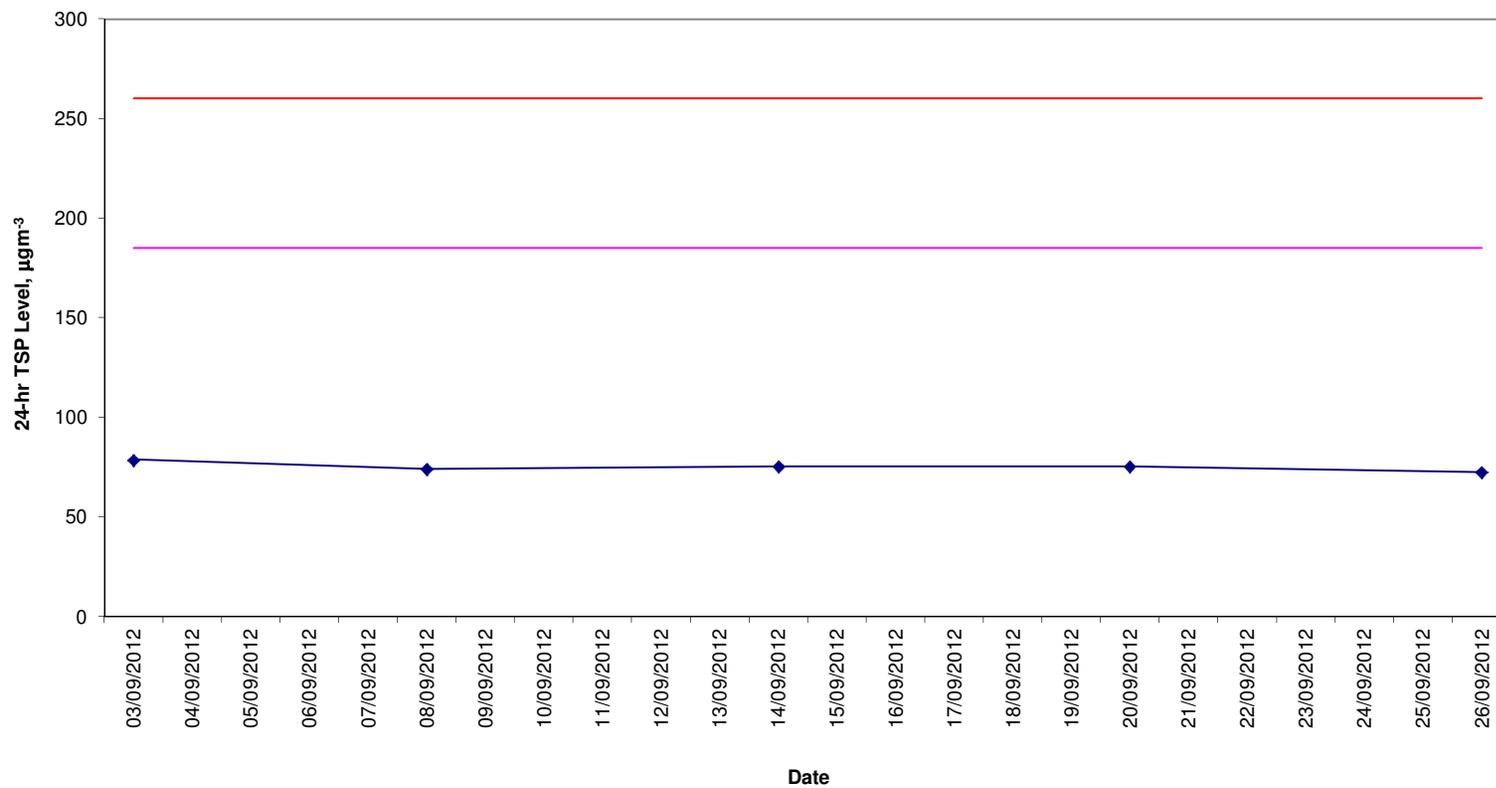

Meteorological Data Extracted from the Hong Kong Observatory

Date	Weather	King's Park Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	5	SE
4/9/2012	Sunny	27	86	17.5	7	E
6/9/2012	Sunny	29	81	2.5	8	E
8/9/2012	Sunny	28.4	79.0	12.0	Not available	Not available
12/9/2012	Sunny	29	78	0.0	9.0	SE
14/9/2012	Sunny	26	63	0.0	9.0	NE
20/9/2012	Sunny	27	79	0.5	Maintenance	E
24/9/2012	Cloudy	32	88	105.0	Maintenance	SE
25/9/2012	Sunny	27	82	20.5	Maintenance	Maintenance
26/9/2012	Cloudy	29	79	0.0	Maintenance	Maintenance
28/9/2012	Sunny	31	53	0.0	18.0	NE
29/9/2012	Sunny	30.8	56.0	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	8.3	N

Date	Weather	Tsing Yi Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	27	77	0.0	10	E
4/9/2012	Sunny	28	86	17.5	9	E
6/9/2012	Sunny	30	81	2.5	5	SE
8/9/2012	Sunny	26	79	12.0	Not available	Not available
12/9/2012	Sunny	30	78	0.0	15.0	NE
14/9/2012	Sunny	27	63	0.0	9.0	NW
20/9/2012	Sunny	28	79	0.5	2.0	E
24/9/2012	Cloudy	27	88	105.0	6.0	E
25/9/2012	Sunny	27	82	20.5	8	E
26/9/2012	Cloudy	27	79	0.0	3.0	NE
28/9/2012	Sunny	29	53	0.0	9.0	NW
29/9/2012	Sunny	32	56	0.0	8.0	NW
30/9/2012	Sunny	27	61	0.0	8.0	NW

Date	Weather	Kai Tak Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	12	SE
4/9/2012	Sunny	27	86	17.5	15	E
6/9/2012	Sunny	29	81	2.5	9	NE
8/9/2012	Sunny	28	79	12.0	Not available	Not available
12/9/2012	Sunny	29	78	0.0	10.0	SE
14/9/2012	Sunny	26	63	0.0	12.0	NW
20/9/2012	Sunny	27	79	0.5	16.0	E
24/9/2012	Cloudy	32	88	105.0	6.0	SE
25/9/2012	Sunny	27	82	20.5	20.0	E
26/9/2012	Cloudy	29	79	0.0	5.0	E
28/9/2012	Sunny	31	53	0.0	18.0	N
29/9/2012	Sunny	31	56	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	9.7	N

Date	Weather	Green Island Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	15	NE
4/9/2012	Sunny	27	86	17.5	25	NE
6/9/2012	Sunny	29	81	2.5	30	NE
8/9/2012	Sunny	28	79	12.0	20	Not available
12/9/2012	Sunny	29	78	0.0	9	SE
14/9/2012	Sunny	26	63	0.0	30	N
20/9/2012	Sunny	27	79	0.5	27	NE
24/9/2012	Cloudy	32	88	105.0	8	S
25/9/2012	Sunny	27	82	20.5	35	NE
26/9/2012	Cloudy	29	79	0.0	12	SE
28/9/2012	Sunny	31	53	0.0	25	N
29/9/2012	Sunny	31	56	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	19	N

- \* King's Park's data
- Data were not available
- # less than 24 hourly observations per day



## Annex C6 Noise Monitoring Results


### Restricted Hours Noise Monitoring Results <sup>[1]</sup>

#### Station NM1

Date	Start Time	End Time	Weather	Noise level (dB(A)), 5 min			Major Construction Noise Source(s) Observed	Other Noise Source(s) Observed	Remarks	Temp. (°C)	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
				Leq	L10	L90							
2-Sep-12	10:37	10:42	Sunny	68.4	70.2	65.3	Noise from nearby playground	Mainly traffic noise	-	32	0.3	RION- NL52 (S/N 00710259)	RION - NC73 (S/N 10997142)
	10:42	10:47	Sunny	69.7	71.1	66.2			-				
	10:47	10:52	Sunny	69.5	70.9	65.9			-				
	10:37	10:52	Sunny	69.2	70.8	65.8			-				
11-Sep-12	19:12	19:17	Fine	67.9	70.4	64.6	-	Mainly traffic noise	-	34	0.3	RION- NL52 (S/N 00710259)	RION - NC73 (S/N 10997142)
	19:17	19:22	Fine	67.6	70.8	65.0			-				
	19:22	19:27	Fine	68.0	71.0	64.3			-				
	19:12	19:27	Fine	67.8	70.7	64.6			-				
16-Sep-12	11:00	11:05	Sunny	68.5	71.2	66.1	-	Mainly traffic noise	-	30	0.5	RION- NL52 (S/N 00710259)	RION - NC73 (S/N 10997142)
	11:05	11:10	Sunny	68.1	70.5	66.3			-				
	11:10	11:15	Sunny	68.3	71.0	66.3			-				
	11:00	11:15	Sunny	68.3	70.9	66.2			-				
25-Sep-12	21:03	21:08	Fine	67.1	69.0	63.0	Noise from nearby playground	Mainly traffic noise	-	27	0.3	RION- NL31 (S/N 00603867)	RION - NC73 (S/N 10997142)
	21:08	21:13	Fine	62.5	69.5	63.5			-				
	21:13	21:18	Fine	67.2	69.0	63.5			-				
	21:03	21:18	Fine	66.1	69.2	63.3			-				
30-Sep-12	10:15	10:20	Sunny	67.5	70.2	64.2	Noise from nearby playground	Mainly traffic noise	-	24	0.3	RION- NL31 (S/N 00603867)	RION - NC73 (S/N 10997142)
	10:20	10:25	Sunny	68.2	71.1	64.5			-				
	10:25	10:30	Sunny	67.6	70.5	64.1			-				
	10:15	10:30	Sunny	67.8	70.6	64.3			-				
			<b>Min.</b>	<b>62.5</b>									
			<b>Max.</b>	<b>69.7</b>									


[1] No class was held at the school during all of the monitoring sessions within the reporting month.

Normal Weekdays Noise Monitoring Results at NM1 ( $L_{eq, 30min}$ )

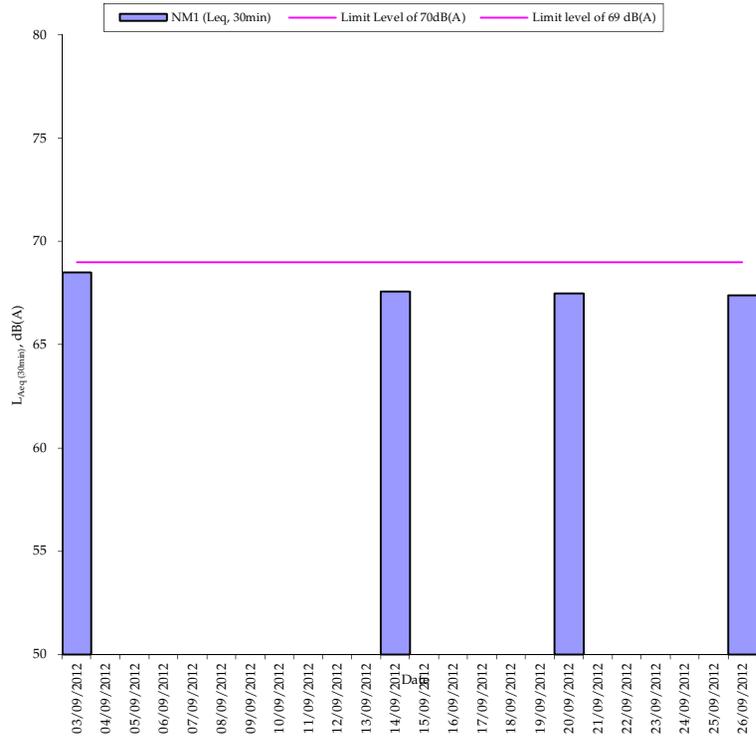

Remark:  
 - 70dB(A) was adopted as the Limit Level during school normal teaching period in the reporting period

Restricted Hours Noise Monitoring Results at NM1 ( $L_{eq, 5min}$ )

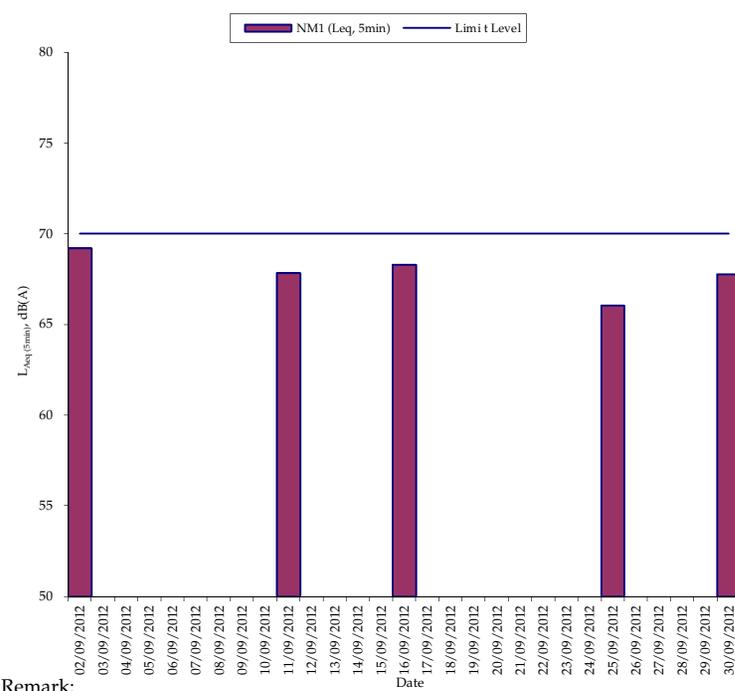

Remark:  
 - No class was held at the school during all the measurement period.  
 - 70dB(A) was adopted as the Limit Level during restricted hours in the reporting period  
 - 55dB(A) was adopted as the Limit Level during night time period

*Annex C7 Cumulative Complaint and Summons/Prosecutions Log*

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
December 2009	0	0
January 2010	0	0
February 2010	0	0
March 2010	0	0
April 2010	0	0
May 2010	0	0
June 2010	0	0
July 2010	0	0
August 2010	0	0
September 2010	0	0
October 2010	0	0
November 2010	0	0
December 2010	0	0
January 2011	0	0
February 2011	0	0
March 2011	0	0
April 2011	0	0
May 2011	0	0

*Annex C7 Cumulative Complaint and Summons/Prosecutions Log*

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
June 2011	0	0
July 2011	0	0
August 2011	0	0
September 2011	0	0
October 2011	0	0
November 2011	0	0
December 2011	0	0
January 2012	0	0
February 2012	0	0
March 2012	0	0
April 2012	0	0
May 2012	0	0
June 2012	0	0
July 2012	0	0
August 2012	0	0
September 2012	0	0
Overall Total	0	0





Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	% Comp	2010					2011					2012					2013					2014																																	
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
<b>HATS Stage 2A - Contract DC/2007/23</b>																																																											
<b>North Point PTW Drop Shaft</b>																																																											
<b>EBS, Env. &amp; Geotechnical Instrumentations</b>																																																											
Markers/UMP's/Others(Same note as Piez.)																																																											
NPDS0263	NPDS: Install SS Markers (22 Nos.)	50	19OCT09A	02FEB10	76						NPDS: Install SS Markers (22 Nos.)																																																
NPDS0264	NPDS: JointSurvey&EstablishBaseline Readings SSM	14	03FEB10	22FEB10	0						NPDS: JointSurvey&EstablishBaseline Readings SSM																																																
Piezometers(NearbyPTWorPScovers in thisInstalln)																																																											
NPDS0280	NPDS: Installation Works of BH800 Piezometer	21	18JAN10A	10FEB10	10						NPDS: Installation Works of BH800 Piezometer																																																
NPDS0290	NPDS: BH800 Piezometer Baseline Establishment	26	11FEB10	16MAR10	0						NPDS: BH800 Piezometer Baseline Establishment																																																
NPDS0383	NPDS: Installation Works of BH801 Piezometer	21	18JAN10A	10FEB10	10						NPDS: Installation Works of BH801 Piezometer																																																
NPDS0385	NPDS: BH801 Piezometer Baseline Establishment	26	11FEB10	16MAR10	0						NPDS: BH801 Piezometer Baseline Establishment																																																
NPDS0391	NPDS: BH802 Piezometer Baseline Establishment	26	23DEC09A	04FEB10	46						NPDS: BH802 Piezometer Baseline Establishment																																																
NPDS0395	NPDS: Installation Works of BH803 Piezometer	21	18JAN10A	10FEB10	10						NPDS: Installation Works of BH803 Piezometer																																																
NPDS0397	NPDS: BH803 Piezometer Baseline Establishment	26	11FEB10	16MAR10	0						NPDS: BH803 Piezometer Baseline Establishment																																																
NPDS0401	NPDS: Installation Works of BH916 Piezometer	21	28DEC09A	11FEB10	5						NPDS: Installation Works of BH916 Piezometer																																																
NPDS0403	NPDS: BH916 Piezometer Baseline Establishment	26	12FEB10	17MAR10	0						NPDS: BH916 Piezometer Baseline Establishment																																																
<b>Diversion of Existing Utilities</b>																																																											
NPDS0100	Provide perma-salt water supply to exis-toi faci	18	09AUG12	29AUG12	0											Provide perma-salt water supply to exis-toi faci																																											
<b>Marine Dumping Permit</b>																																																											
NPDS0212	NPDS: EPD Approved of SQR	24	24NOV09A	27JAN10	70						NPDS: EPD Approved of SQR																																																
NPDS0213	NPDS: Request for Disposal Site & Get Permit	24	28JAN10	27FEB10	0						NPDS: Request for Disposal Site & Get Permit																																																
<b>Pipe Piling</b>																																																											
NPDS0305	NPDS: Pipe Piling Works	110	19JAN10A	27MAY10	5						NPDS: Pipe Piling Works																																																
NPDS0310	NPDS: Grouting for PP Wall	75	31MAR10	29JUN10	0						NPDS: Grouting for PP Wall																																																
NPDS0320	NPDS: Install Temp Steel Casing	76	30JUN10	28SEP10	0						NPDS: Install Temp Steel Casing																																																
NPDS0330	NPDS: Grouting for Temp Casing	40	29SEP10	16NOV10	0						NPDS: Grouting for Temp Casing																																																
NPDS0340	NPDS: Install Dewatering Wells for Pump-test	12	08NOV10	20NOV10	0						NPDS: Install Dewatering Wells for Pump-test																																																
NPDS0350	NPDS: Pumping Test	6	22NOV10	27NOV10	0						NPDS: Pumping Test																																																
NPDS0360	NPDS: Submission of Pumping Test Report	6	29NOV10	04DEC10	0						NPDS: Submission of Pumping Test Report																																																
NPDS0370	NPDS: Demobilization for PP Wall	6	29NOV10	04DEC10	0						NPDS: Demobilization for PP Wall																																																
<b>Shaft Excavation</b>																																																											
NPDS0400	NPDS: Construct Capping Beam & Shaft Collar	12	27NOV10	10DEC10	0						NPDS: Construct Capping Beam & Shaft Collar																																																
NPDS0450	NPDS: Drawdown water & Excavate below S2 Level	5	11DEC10	16DEC10	0						NPDS: Drawdown water & Excavate below S2 Level																																																
NPDS0460	NPDS: Construct S2 Ring Beam	2	17DEC10	18DEC10	0						NPDS: Construct S2 Ring Beam																																																
NPDS0470	NPDS: Drawdown water & Excavate below S3 Level	4	20DEC10	23DEC10	0						NPDS: Drawdown water & Excavate below S3 Level																																																
NPDS0480	NPDS: Construct S3 Ring Beam	2	24DEC10	27DEC10	0						NPDS: Construct S3 Ring Beam																																																
NPDS0490	NPDS: Drawdown water & Excavate below S4 Level	4	28DEC10	31DEC10	0						NPDS: Drawdown water & Excavate below S4 Level																																																
NPDS0500	NPDS: Construct S4 Ring Beam	2	03JAN11	04JAN11	0						NPDS: Construct S4 Ring Beam																																																
NPDS0510	NPDS: Drawdownwater &Excav.to-8.5mPD Final Level	3	05JAN11	07JAN11	0						NPDS: Drawdownwater &Excav.to-8.5mPD Final Level																																																
NPDS0512	NPDS: Construct Levelling Pad	6	08JAN11	14JAN11	0						NPDS: Construct Levelling Pad																																																
NPDS0514	NPDS: Pre-excavation Grout for Raise Bore	90	15JAN11	05MAY11	0						NPDS: Pre-excavation Grout for Raise Bore																																																
NPDS0516	NPDS: In-fill Concrete for Pilot Hole	12	06MAY11	19MAY11	0						NPDS: In-fill Concrete for Pilot Hole																																																
NPDS0800	NPDS: Complete Excav. to Rockhead at NP DS(KD-A)	0	07JAN11	07JAN11	0						NPDS: Complete Excav. to Rockhead at NP DS(KD-A)																																																
NPDS0810	NPDS: Compl PP Wall, Soil Excav&Clear Area(KD- 01)	0	07JAN11	07JAN11	0						NPDS: Compl PP Wall, Soil Excav&Clear Area(KD- 01)																																																
<b>Raised Boring</b>																																																											
NPDS0700	NPDS: Rig Up Hole 1	5	12SEP11	17SEP11	0											NPDS: Rig Up Hole 1																																											
NPDS0710	NPDS: Pilot Drill 121 mtrs	15	19SEP11	07OCT11	0											NPDS: Pilot Drill 121 mtrs																																											
NPDS0720	NPDS: Attach Reamer and Collar	3	08OCT11	11OCT11	0											NPDS: Attach Reamer and Collar																																											
NPDS0730	NPDS: Ream 121 metres @ 2.8 mtr dia	32	12OCT11	17NOV11	0											NPDS: Ream 121 metres @ 2.8 mtr dia																																											
NPDS0740	NPDS: Lower Reamer and Remove	3	18NOV11	21NOV11	0											NPDS: Lower Reamer and Remove																																											
NPDS0750	NPDS: De Rig Raise borer and Re rig Hole 2	5	22NOV11	26NOV11	0											NPDS: De Rig Raise borer and Re rig Hole 2																																											
NPDS0760	NPDS: Pilot Drill 121 mtrs	15	28NOV11	14DEC11	0											NPDS: Pilot Drill 121 mtrs																																											
NPDS0770	NPDS: Attach Reamer and collar	3	15DEC11	17DEC11	0											NPDS: Attach Reamer and collar																																											
NPDS0780	NPDS: Ream 121 metres @ 2.8 mtr dia	32	19DEC11	30JAN12	0											NPDS: Ream 121 metres @ 2.8 mtr dia																																											
NPDS0790	NPDS: De Rig Raise Borer & Remove Reamer	3	31JAN12	02FEB12	0											NPDS: De Rig Raise Borer & Remove Reamer																																											
<b>Lower Shaft Construction</b>																																																											
NPDS0895	NPDS: Blinding Layer & Concrete Shaft Base	6	03FEB12	09FEB12	0											NPDS: Blinding Layer & Concrete Shaft Base																																											
NPDS0900	NPDS: Back shunt concreting	18	10FEB12	01MAR12	0											NPDS: Back shunt concreting																																											
NPDS0905	NPDS: Construct Verti-Shaft to Tunnel Invert	6	02MAR12	08MAR12	0											NPDS: Construct Verti-Shaft to Tunnel Invert																																											
NPDS0955	NPDS: Install System Form for Lower Shaft	6	09MAR12	15MAR12	0											NPDS: Install System Form for Lower Shaft																																											
NPDS0995	NPDS: Construct Transition & Vert Shaft	9	16MAR12	26MAR12	0											NPDS: Construct Transition & Vert Shaft																																											
NPDS1015	NPDS: Construct lower-shaft -159.5 to -8.5mPD	80	27MAR12	30JUN12	0											NPDS: Construct lower-shaft -159.5 to -8.5mPD																																											
NPDS1020	NPDS: Remove system formwork and tidy up area	6	03JUL12	09JUL12	0											NPDS: Remove system formwork and tidy up area																																											
<b>Upper Shaft Construction</b>																																																											
NPDS1025	NPDS: Blinding Layer & Construct Base Slab	9	10JUL12	19JUL12	0											NPDS: Blinding Layer & Construct Base Slab																																											
NPDS1065	NPDS: Temp Platform & Construct Conical Surface	6	20JUL12	26JUL12	0											NPDS: Temp Platform & Construct Conical Surface																																											
NPDS1110	NPDS: Assembly of kicker frmwork	12	27JUL12	09AUG12	0											NPDS: Assembly of kicker frmwork																																											
NPDS1135	NPDS: Construct Kicker	9	10AUG12	20AUG12	0											NPDS: Construct Kicker																																											
NPDS1140	NPDS: Set up system formwork for upper shaft	16	10AUG12	28AUG12	0											NPDS: Set up system formwork for upper shaft																																											
NPDS1145	NPDS: Construct Upper Shaft	44	29AUG12	20OCT12	0											NPDS: Construct Upper Shaft																																											
NPDS1305	NPDS: Fabricate & Install S/S Vortex Drop Pipe	12	15OCT12	29OCT12	0											NPDS: Fabricate & Install S/S Vortex Drop Pipe																																											
NPDS1345	NPDS: Construct Overflow Weir	6	30OCT12	05NOV12	0											NPDS: Construct Overflow Weir																																											
NPDS1385	NPDS: Insta Preca Downpp NP2 & Concrte Enclosure	9	06NOV12	15NOV12	0											NPDS: Insta Preca Downpp NP2 & Concrte Enclosure																																											
NPDS1395	NPDS: Clear Area & Install Multi-Part Cover	3	16NOV12	19NOV12	0											NPDS: Clear Area & Install Multi-Part Cover																																											
<b>Scum Removal Chamber</b>																																																											
NPDS1533	NPDS: Sheet Piling, Excavation & ELS Works	24	21SEP12	20OCT12	0											NPDS: Sheet Piling, Excavation & ELS Works																																											
NPDS1545	NPDS: Excavation for Chamber & Channel	9	22OCT12	01NOV12	0											NPDS: Excavation for Chamber & Channel																																											
NPDS1585	NPDS: Blinding Layer & Construct Base Slab of SRC	9	02NOV12	12NOV12	0											NPDS: Blinding Layer & Construct Base Slab of SRC																																											
NPDS1625	NPDS: Construct Wall of SRC	9	13NOV12	22NOV12	0											NPDS: Construct Wall of SRC																																											
NPDS1645	NPDS: Waterproof & Insta Multi-Part Cover of SRC	6	23NOV12	29NOV12	0											NPDS: Waterproof & Insta Multi-Part Cover of SRC																																											
NPDS1650	NPDS: Backfill	3	30NOV12	03DEC12	0											NPDS: Backfill																																											
<b>Connection Channel</b>																																																											
NPDS1455	NPDS: Blinding Layer & Construct Base Slab for CC	9	02NOV12	12NOV12	0											NPDS: Blinding Layer & Construct Base Slab for CC																																											
NPDS1515	NPDS: Construct Wall of CC	12	13NOV12	26NOV12	0											NPDS: Construct Wall of CC																																											

Start Date	31JUL09	Early Bar
Finish Date	15JAN15	Progress Bar
Data Date	20JAN10	Critical Activity
Run Date	01FEB10 09:50	

WPU7 Sheet 1 of 2

**Habour Area Treatment Scheme Stage 2A**  
**Contract No. DC/2007/23 - Construction of Sewage**  
**Conveyance from North Point to Stonecutters Island**  
**Programme**

Annex C8 Construction Programme for the Project

Date	Revision	Checked/Approved



Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	% Comp	2010												2011												2012												2013												2014												
NPDS1525	NPDS: Waterproof & Insta Multi-Part Cover of CC	6	27NOV12	03DEC12	0																																																													NPDS: Waterproof & Insta Multi-Part Cover of CC
NPDS1540	NPDS: Backfill	3	04DEC12	06DEC12	0																																																													NPDS: Backfill
Miscellaneous Works																																																																		
NPDS2010	NPDS: Install E&M Services	18	14FEB13	06MAR13	0																																																													NPDS: Install E&M Services
NPDS2020	NPDS: Reinstatement & Clear DS Area	12	07MAR13	20MAR13	0																																																													NPDS: Reinstatement & Clear DS Area
NPDS2025	NPDS: Complete All Works at NP DS(KD-05)	0		20MAR13	0																																																													NPDS: Complete All Works at NP DS(KD-05)
NPDS2030	NPDS: Landscaping & Planting Works	60	21MAR13*	19MAY13	0																																																													NPDS: Landscaping & Planting Works
NPDS2040	NPDS: Period of Establishment Works	360	20MAY13	14MAY14	0																																																													NPDS: Period of Establishment Works
NPDS2050	NPDS: End of Establishment Period	0		14MAY14	0																																																													NPDS: End of Establishment Period

Start Date 31JUL09  
 Finish Date 15JAN15  
 Data Date 20JAN10  
 Run Date 01FEB10 09:50

 Early Bar  
 Progress Bar  
 Critical Activity

WPU7 Sheet 2 of 2  
**Harbour Area Treatment Scheme Stage 2A**  
 Contract No. DC/2007/23 - Construction of Sewage  
 Conveyance from North Point to Stonecutters Island  
 Programme  
 Annex C8 Construction Programme for the Project




Date	Revision	Checked	Approved

Annex D

## Wan Chai East Production and Drop Shafts

**Key**

-  Shaft Excavation Location
-  Site Location

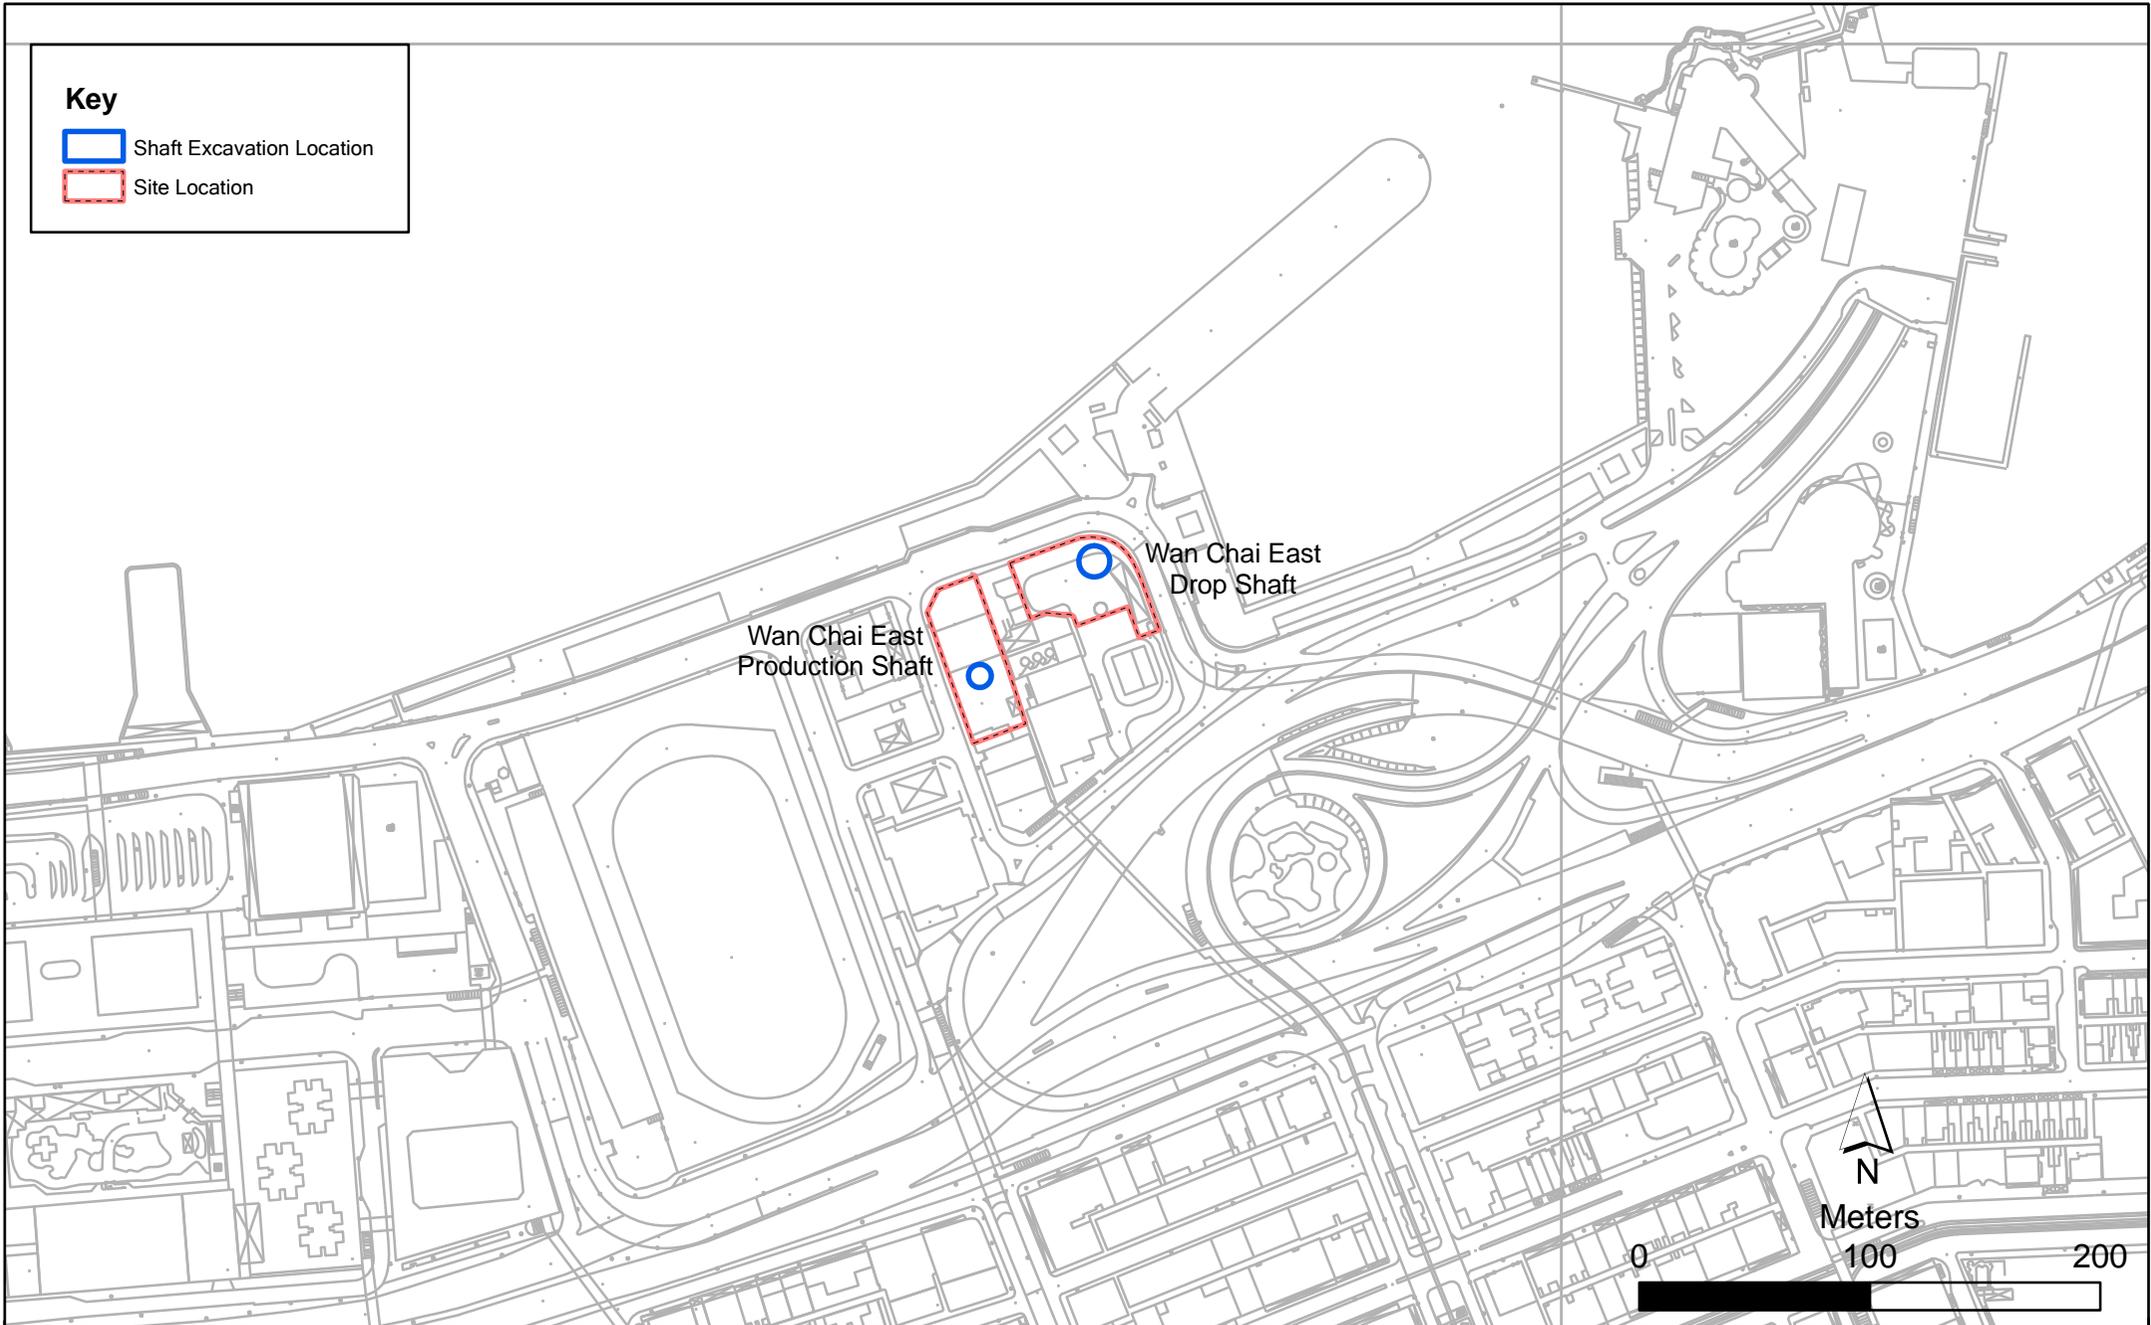

Annex D1

Contract No. DC/2007/23  
Harbour Area Treatment Scheme Stage 2A  
Construction of Sewage Conveyance System from North Point to Stonecutters Island  
*Construction Site Locations at Wai Chai East*

File: EM&A and proposed station\0104887\_Wan Chai.mxd  
Date: 29/10/2009

Environmental  
Resources  
Management



**Key**


-  Air Quality Monitoring Station
-  Noise Monitoring Station
-  Shaft Excavation Location
-  Site Location

**Air Quality Monitoring Station**

AM3 Rooftop of Wan Chai East PTW

**Noise Monitoring Station**

NM2 Hyde Building

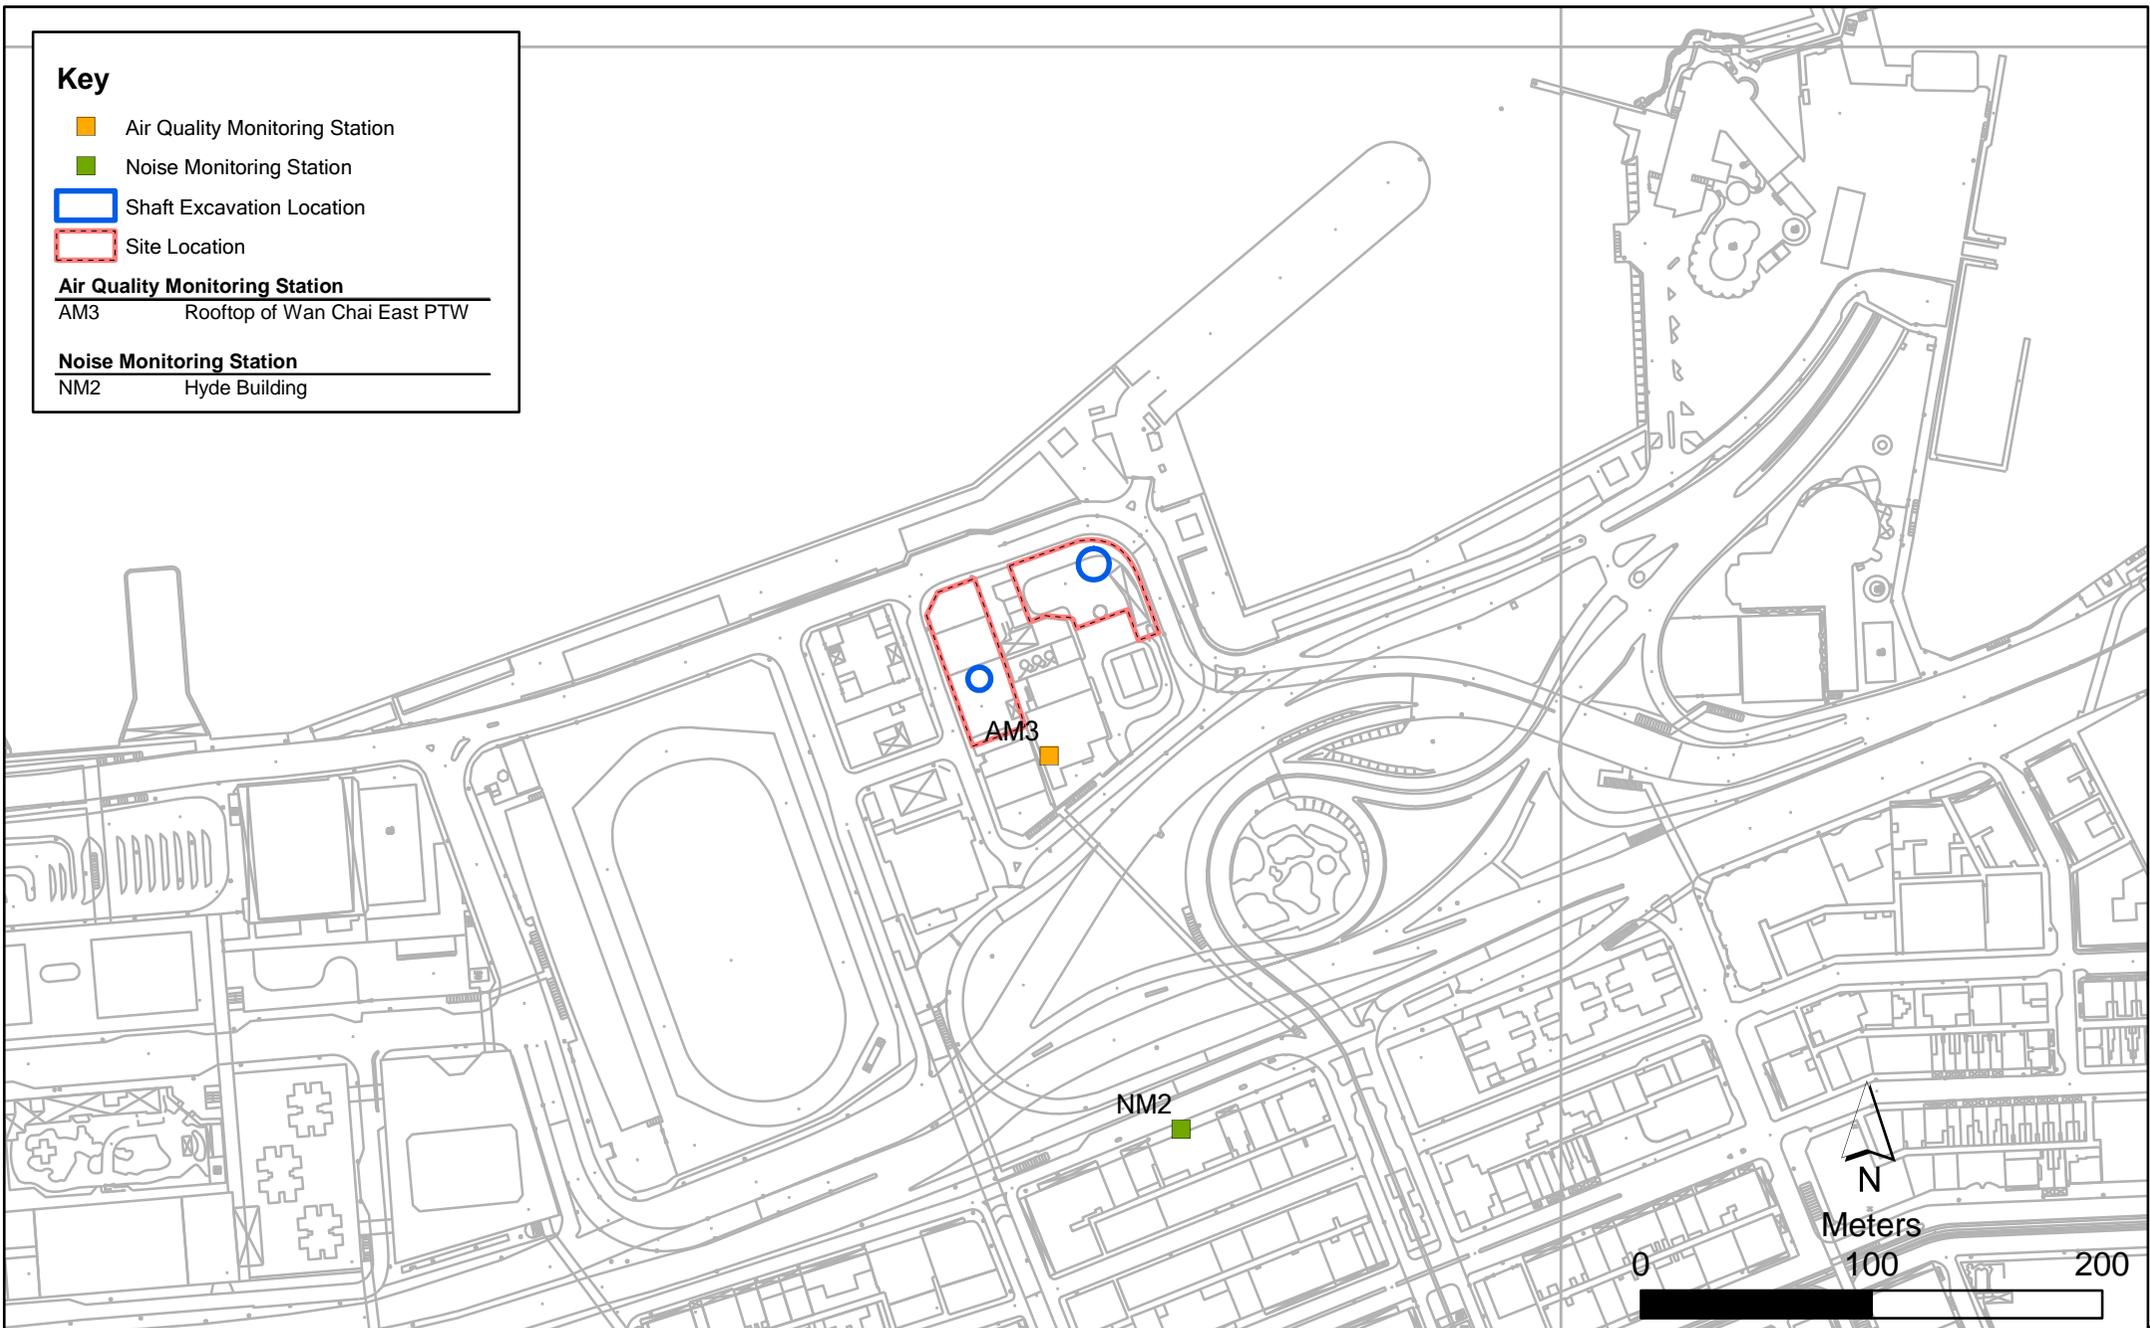

## Annex D3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23  
 Harbour Area Treatment Scheme Stage 2A  
 Construction of Sewage Conveyance System from North Point to Stonecutters Island  
 Impact Construction Air Quality Monitoring Schedule

**AM3 - Wan Chai East PTW**  
**Monitoring Month : September 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
	1-hr and 24-hr Monitoring					1-hr and 24-hr Monitoring
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
					1-hr and 24-hr Monitoring	
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
				1-hr and 24-hr Monitoring		
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
			1-hr and 24-hr Monitoring			1-hr and 24-hr Monitoring
30-Sep						

**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
	Public Holiday	Public Holiday			1-hr and 24-hr Monitoring	
7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
				1-hr and 24-hr Monitoring		
14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
			1-hr and 24-hr Monitoring			
21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct
	1-hr and 24-hr Monitoring	Public Holiday				1-hr and 24-hr Monitoring
28-Oct	29-Oct	30-Oct	31-Oct			

# Annex D3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23

Harbour Area Treatment Scheme Stage 2A

Construction of Sewage Conveyance System from North Point to Stonecutters Island

Impact Construction Noise Quality Monitoring Schedule

**NM2 - Hyde Building**

**Monitoring Month : September 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
Noise Monitoring (during daytime of sundays/ public holidays)	Noise Monitoring					
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
		Noise Monitoring (evening time)			Noise Monitoring	
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
Noise Monitoring (during daytime of sundays/ public holidays)				Noise Monitoring		
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
		Noise Monitoring (evening time)	Noise Monitoring			
30-Sep						
Noise Monitoring (during daytime of sundays/ public holidays)						



**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
	Public Holiday	Public Holiday			Noise Monitoring	
7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
		Noise Monitoring (evening time)		Noise Monitoring		
14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
Noise Monitoring (during daytime of sundays/ public holidays)			Noise Monitoring			
21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct
	Noise Monitoring	Noise Monitoring (Evening time) Public Holiday				
28-Oct	29-Oct	30-Oct	31-Oct			
Noise Monitoring (during daytime of sundays/ public holidays)						

**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Construction Phase</i>			
Air Quality	<p>The Air Pollution Control (Construction Dust) Regulation shall be implemented and good site practices shall be incorporated in the contract clauses to minimize construction dust impact. Control measures relevant to this Project are listed below:</p> <ul style="list-style-type: none"> <li>• skip hoist for material transport should be totally enclosed by impervious sheeting;</li> <li>• every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site;</li> <li>• the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;</li> <li>• where a site boundary adjoins a road, streets or other accessible to the public, hoarding of not less than 2.4 m high from ground level should be provided along the entire length except for a site entrance or exit;</li> <li>• every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the 3 sides;</li> <li>• regular watering, with complete coverage, to reduce dust emission from exposed site surfaces and unpaved roads, particularly during dry weather;</li> <li>• site enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines;</li> <li>• open stock piles should be avoided or covered and prevent placing dusty material storage piles near ASRs if possible;</li> <li>• tarpaulin covering of all dusty vehicle loads transported to, from and between site locations; and</li> <li>• instigation of an environmental monitoring auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.</li> </ul>	All work sites / during construction	<>

**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Air Quality	<p>The following watering measures for specific site would be required to control the fugitive dust impacts:</p> <ul style="list-style-type: none"> <li>• watering twice per day within the worksites at Wan Chai East PTW;</li> <li>• the barging points should be continuous watering throughout the whole unloading process; and</li> <li>• watering 8 times per day within worksites at the SCS works area at Wan Chai East.</li> </ul>	All work sites / during construction	√
<i>Operational Phase</i>			
Air Quality	<p>Good housekeeping for SCISTW and PTWs listed below should be followed to ameliorate any odour impact from the plant and these standard practices should be included in the plant operator manual.</p> <ul style="list-style-type: none"> <li>• Screens should be cleaned regularly to remove any accumulated organic debris</li> <li>• Grit and screening transfer systems should be flushed regularly with water to remove organic debris and grit</li> <li>• Grit and screened materials should be transferred to closed containers to minimize odour escape</li> <li>• Scum and grease collection wells and troughs should be emptied and flushed regularly to prevent putrefaction of accumulated organics</li> <li>• Skim and remove floating solids and grease from primary clarifiers regularly</li> <li>• Frequent sludge withdrawal from tanks is necessary to prevent the production of gases</li> <li>• Sludge cake should be transferred to closed containers</li> <li>• Sludge containers should be flushed with water regularly</li> </ul>	All work sites / during construction	NA. Measures not required until commencement of operational phase
Air Quality	Commissioning tests for all deodorization system should be included in the Design and Construction Contract Document.	All PTW and SCISTW/ during operational phase	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			
Noise	Use of quiet PME, movable barriers and acoustic mats	All work sites / during construction	√

**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Noise	<p>Good Site Practice:</p> <ul style="list-style-type: none"> <li>• only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program;</li> <li>• silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program;</li> <li>• mobile plant, if any, should be sited as far from NSRs as possible;</li> <li>• machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;</li> <li>• plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>• material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities;</li> </ul> <p>Environmental audit shall be carried out to ensure that appropriate noise control measures would be properly implemented.</p>	All work sites / during construction	√
<i>Construction Phase</i>			
Water Quality	<p>Construction Site Runoff and General Construction Activities</p> <p>The mitigation measures as outlined in the ProPECC PN 1/94 Construction Site Drainage should be adopted where applicable.</p>	All work sites / during construction	√

**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Effluent Discharge</p> <p>There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD. Minimum distances of 100 m should be maintained between the discharge points of construction site effluent and the existing saltwater intakes.</p>	All work sites / during construction	√
Water Quality	<p>Accidental Spillage of Chemicals</p> <p>Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.</p>	All work sites / during construction	√
Water Quality	<p>Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.</p>	All work sites / during construction	<>

**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes.</p> <p>General requirements are given as follows:</p> <ul style="list-style-type: none"> <li>• Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</li> <li>• Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents.</li> <li>• Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.</li> </ul>	All work sites / during construction	√

**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Construction Works in Close Proximity of Storm Drains or Seafront</p> <p>To minimize the potential water quality impacts from the construction works located at or near any watercourse, the practices outlined below should be adopted where applicable.</p> <ul style="list-style-type: none"> <li>• The use of less or smaller construction plants may be specified to reduce the disturbance to the storm water courses or marine environment.</li> <li>• Temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works.</li> <li>• Stockpiling of construction materials and dusty materials should be covered and located away from any water courses.</li> <li>• Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers.</li> <li>• Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the waterfront, where practicable.</li> <li>• Proper shoring may need to be erected in order to prevent soil/mud from slipping into the storm culvert or sea</li> </ul>	All work sites / during construction	√

**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Operational Phase</i>			
Water Quality	Dual power supply, standby facilities for the main treatment units and standby equipment parts / accessories should be provided as far as possible at the SCISTW to minimize the chance of emergency discharge.	SCISTW and all the Stage 2 PTWs / Operation Stage	NA. Measures not required until commencement of operational phase
Water Quality	Standby unit(s) and dual (backup) power supply would be provided at all the Stage 2 PTWs to reduce the risk of equipment breakdown at the PTWs.	Stage 2 PTWs / Operation Stage	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			
Waste	Reusable steel or concrete panel shutters, fencing and hoarding and signboard should be used as a preferred alternative to items made of wood, to minimise wastage of wood. Attention should be paid to WBTC No. 19/2001 - Metallic Site Hoardings and Signboards to reduce the amount of timber used on construction sites. Metallic alternatives to timber are readily available and should be used rather than new timber. Precast concrete units should be adopted wherever feasible to minimize the use of timber formwork.	All work sites / during the construction period	√
Waste	All waste materials should be segregated into categories covering: <ul style="list-style-type: none"> <li>• excavated materials suitable for reuse on-site;</li> <li>• excavated materials suitable for public filling facilities;</li> <li>• remaining C&amp;D waste for landfill;</li> <li>• chemical waste; and</li> <li>• general refuse for landfill.</li> </ul>	All work sites / during the construction period	√



**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	<p>Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> <li>• Sort C&amp;D waste from demolition of existing facilities to recover recyclable portions such as metals;</li> <li>• Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>• Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force;</li> <li>• Any unused chemicals or those with remaining functional capacity shall be recycled; and</li> <li>• Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> </ul>	All work sites / during the construction period	√
Waste	<p>Recommendations for good site practices during construction activities include:-</p> <ul style="list-style-type: none"> <li>• Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site</li> <li>• Training of site personnel in proper waste management and chemical waste handling procedures</li> <li>• Develop and provide toolbox talk for on-site sorting of C&amp;D materials to enhance worker’s awareness in handling, sorting, reuse and recycling of C&amp;D materials.</li> <li>• Provision of sufficient waste disposal points and regular collection of waste</li> <li>• Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors</li> </ul>	All work sites / during the construction period	√
Waste	<p>Bentonite slurries used in diaphragm wall construction should be reconditioned and reused wherever practicable. The disposal of residual used bentonite slurry should follow the good practice guidelines stated in ProPECC PN 1/94 “Construction Site Drainage”.</p>	All work sites / during the construction period	√

**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	Adequate number of portable toilets at temporary works areas or the PTWs to ensure that sewage from site staff would be properly collected.	All work sites / during the construction period	√
Waste	General refuse should be stored in enclosed bins, skips or compaction units separating from C&D material and disposed of at designated landfill.	All work sites / during the construction period	√
Waste	The recyclable component of the municipal waste generated by the workforce, such as aluminium cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.	All work sites / during the construction period	√
Waste	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the approved Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	All work sites / during the construction period	√

**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	Prior to excavation of the marine deposit layer, the deposit should be tested in accordance with the ETWB TC(W) No. 34/2002 and the results should be presented in a Preliminary Sediment Quality Report. The marine deposit should be disposed of at the disposal site designated by the Marine Fill Committee (MFC) or Director of Environmental Protection (DEP) depending on the test results.	All work sites / during the construction period	√
<i>Construction Phase</i>			
Landscape & Visual	<ul style="list-style-type: none"> <li>• Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.</li> <li>• Existing trees to be retained on site should be carefully protected during construction.</li> <li>• Trees unavoidably affected by the works should be transplanted where practical.</li> <li>• Compensatory tree planting should be provided to compensate for felled trees.</li> <li>• Control of night-time lighting.</li> <li>• Erection of decorative screen hoarding compatible with the surrounding setting.</li> </ul>	All the works areas, PTWs and SCISTW / during the construction period	√
<i>Operational Phase</i>			
Landscape & Visual	<ul style="list-style-type: none"> <li>• Aesthetic design of the façade of PTW and associated structures to harmonize with the surrounding settings.</li> <li>• Shrub and Climbing Plants to soften proposed structures / Roof Greening.</li> <li>• Buffer Tree and Shrub Planting to screen proposed associated structures.</li> <li>• Reinstated of disturbed area</li> </ul>	All the works areas, PTWs and SCISTW / during the construction period	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			

**ANNEX D4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Cultural Heritage	The construction vibration control limit (ppv of 25mm/s) shall be strictly followed.	Identified historical buildings/ structures as mentioned in Tables 15.8 and 15.9. During blasting for tunnel, shafts, effluent conveyance system and disinfection facilities in the vicinity of the buildings/ structures	NA. Vibration monitoring has not been launched during the reporting period.
	Monitoring of vibration limits shall be conducted and reported as a requirement of EM&A programme	Identified historical buildings/ structures as mentioned in Tables 15.8 and 15.9. During blasting for tunnel, shafts, effluent conveyance system and disinfection facilities in the vicinity of the buildings/ structures	NA. Vibration monitoring has not been launched during the reporting period.

Remark:

- √ Compliance of Mitigation Measures
- <> Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Limited
- NA Not Applicable

## Annex D5 24-hour and 1-hour TSP Monitoring Results

### 1-hour TSP Monitoring Results

#### Station AM3

Date	Start Time	Finish Time	Weather	TSP Concentration ( $\mu\text{g}/\text{m}^3$ )	Action Level ( $\mu\text{g}/\text{m}^3$ )	Limit Level ( $\mu\text{g}/\text{m}^3$ )	Site Conditions / Observations / Remarks	Temperature ( $^{\circ}\text{C}$ )	Wind Speed * (m/s)	Sampler ID	Filter ID
3-Sep-12	12:00	13:00	Sunny	107	355	500	Construction work in progress	32.8	<5	0481	1594
	13:02	14:02	Sunny	104	355	500	Construction work in progress	32.8	<5	0481	1595
	14:04	15:04	Sunny	107	355	500	Construction work in progress	32.8	<5	0481	1611
8-Sep-12	11:41	12:41	Sunny	110	355	500	Construction work in progress	30	<5	0481	1612
	12:47	13:47	Sunny	104	355	500	Construction work in progress	30	<5	0481	1613
	13:49	14:49	Sunny	100	355	500	Construction work in progress	30	<5	0481	1615
14-Sep-12	12:00	13:00	Sunny	103	355	500	Construction work in progress	29	<5	0481	1616
	13:02	14:02	Sunny	118	355	500	Construction work in progress	29	<5	0481	1618
	14:04	15:04	Sunny	104	355	500	Construction work in progress	29	<5	0481	1619
20-Sep-12	12:00	13:00	Cloudy	108	355	500	Construction work in progress	29	<5	0481	1621
	13:02	14:02	Cloudy	104	355	500	Construction work in progress	29	<5	0481	1622
	14:04	15:04	Cloudy	133	355	500	Construction work in progress	29	<5	0481	1624
26-Sep-12	8:00	9:00	Cloudy	82	355	500	Construction work in progress	30	<5	0481	1625
	9:02	10:02	Cloudy	96	355	500	Construction work in progress	30	<5	0481	1627
	10:04	11:04	Cloudy	109	355	500	Construction work in progress	30	<5	0481	1628
29-Sep-12	11:50	12:50	Sunny	163	355	500	Construction work in progress	29	<5	0481	1641
	12:52	13:52	Sunny	96	355	500	Construction work in progress	29	<5	0481	1630
	13:54	14:54	Sunny	187	355	500	Construction work in progress	29	<5	0481	1629
			<b>Min.</b>	<b>82</b>							
			<b>Max.</b>	<b>187</b>							
			<b>Average</b>	<b>113</b>							

\* Wind Speed data is presented in the Meteorological Data table

## Annex D5 24-hour and 1-hour TSP Monitoring Results


### 24-hour TSP Monitoring Results

#### Station AM3

Start		Finish		Weather	Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m <sup>3</sup> /min)			TSP Conc. (µg/m <sup>3</sup> )	Action Level (µg/m <sup>3</sup> )	Limit Level (µg/m <sup>3</sup> )	Observations / Remarks	Sampler ID	Filter ID
Date	Time	Date	Time		Initial	Final	Initial	Final		Initial	Final	Average						
3-Sep-12	15:06	4-Sep-12	15:06	Sunny	2.8201	2.9489	7059.32	7083.32	24.00	1.20	1.20	1.20	75	181	260	Construction work in progress	0481	1596
8-Sep-12	15:00	9-Sep-12	15:00	Sunny	2.8026	2.9196	7086.32	7110.32	24.00	1.20	1.20	1.20	68	181	260	Construction work in progress	0481	1560
14-Sep-12	15:10	15-Sep-12	15:10	Sunny	2.8446	2.9717	7113.32	7137.32	24.00	1.20	1.20	1.20	74	181	260	Construction work in progress	0481	1617
20-Sep-12	15:10	21-Sep-12	15:10	Cloudy	2.8407	2.9696	7140.32	7164.32	24.00	1.22	1.22	1.22	73	181	260	Construction work in progress	0481	1620
26-Sep-12	11:06	27-Sep-12	11:06	Cloudy	2.8285	2.9449	7167.32	7191.32	24.00	1.22	1.22	1.22	66	181	260	Construction work in progress	0481	1623
29-Sep-12	14:56	30-Sep-12	14:56	Sunny	2.8446	3.0008	7194.32	7218.32	24.00	1.22	1.20	1.21	90	181	260	Construction work in progress	0481	1626
													Min.	66				
													Max.	90				
													Average	74				


### 1-hr TSP Levels AM3 (Wan Chai East PTW)

— Action Level — Limit Level ◆ AM3

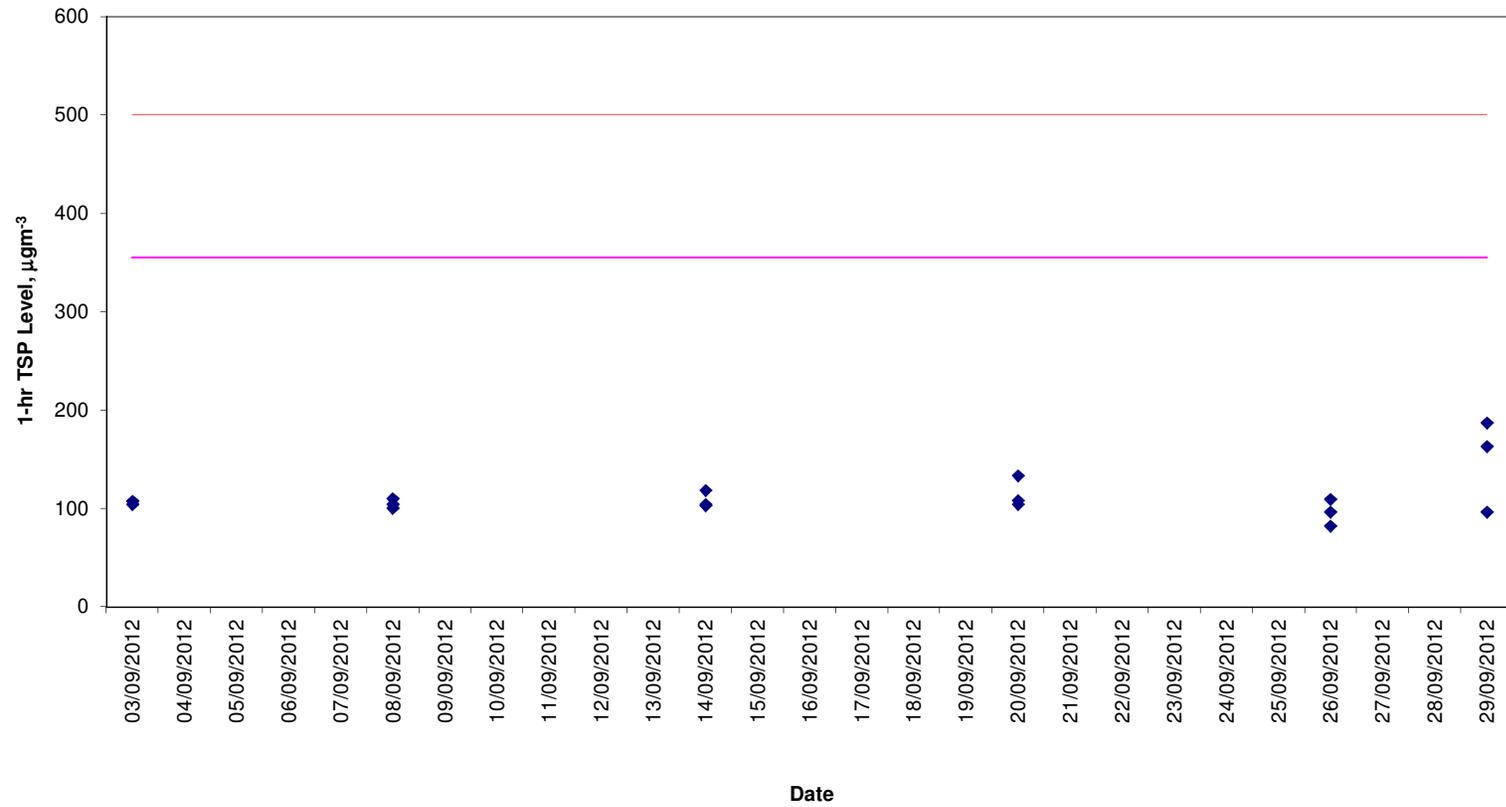

**24-hr TSP Levels  
AM3 (Wan Chai East PTW)**

—◆— AM3    — Action Level    — Limit Level

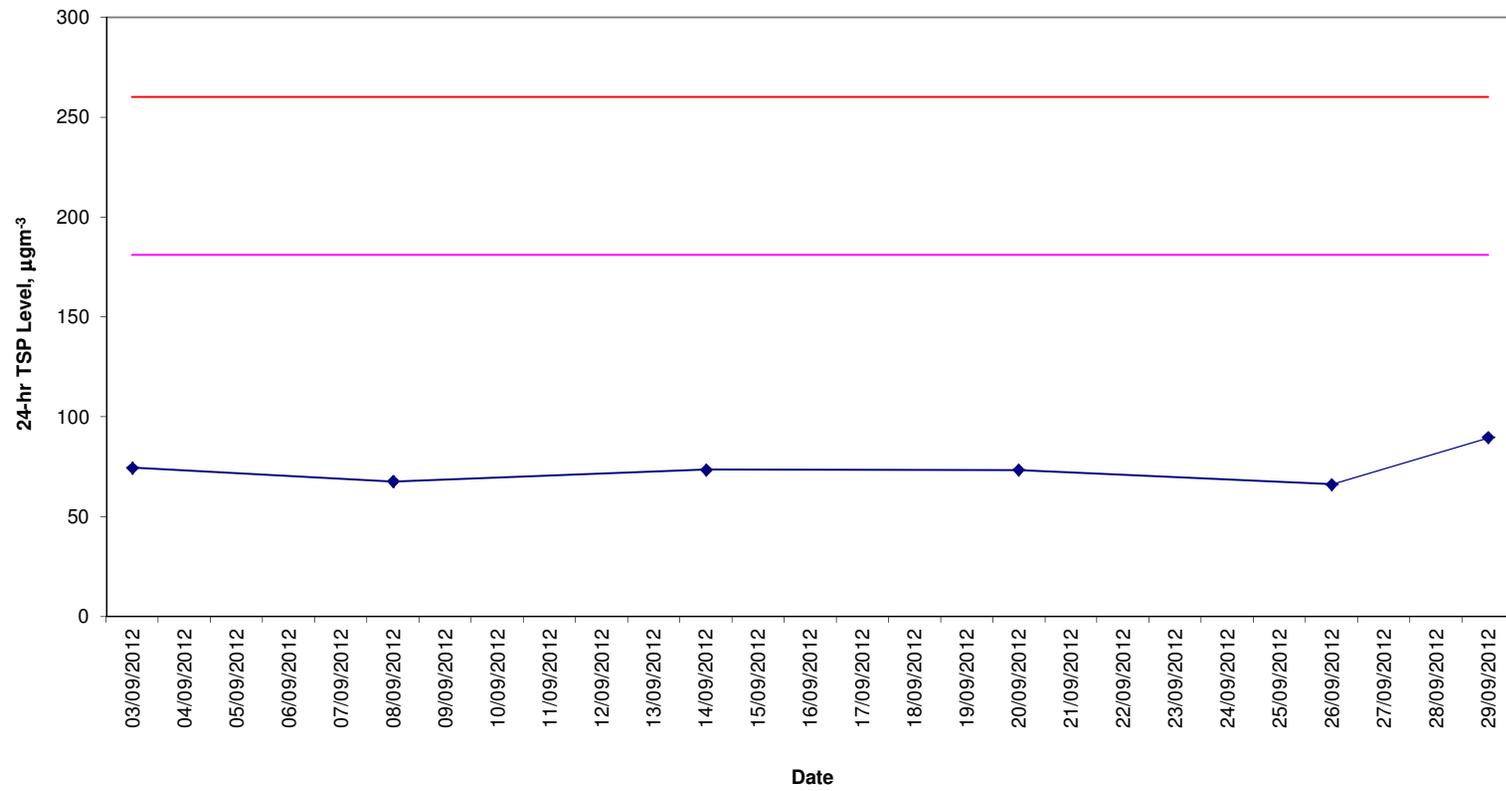



Meteorological Data Extracted from the Hong Kong Observatory

Date	Weather	King's Park Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	5	SE
4/9/2012	Sunny	27	86	17.5	7	E
6/9/2012	Sunny	29	81	2.5	8	E
8/9/2012	Sunny	28.4	79.0	12.0	Not available	Not available
12/9/2012	Sunny	29	78	0.0	9.0	SE
14/9/2012	Sunny	26	63	0.0	9.0	NE
20/9/2012	Sunny	27	79	0.5	Maintenance	E
24/9/2012	Cloudy	32	88	105.0	Maintenance	SE
25/9/2012	Sunny	27	82	20.5	Maintenance	Maintenance
26/9/2012	Cloudy	29	79	0.0	Maintenance	Maintenance
28/9/2012	Sunny	31	53	0.0	18.0	NE
29/9/2012	Sunny	30.8	56.0	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	8.3	N

Date	Weather	Tsing Yi Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	27	77	0.0	10	E
4/9/2012	Sunny	28	86	17.5	9	E
6/9/2012	Sunny	30	81	2.5	5	SE
8/9/2012	Sunny	26	79	12.0	Not available	Not available
12/9/2012	Sunny	30	78	0.0	15.0	NE
14/9/2012	Sunny	27	63	0.0	9.0	NW
20/9/2012	Sunny	28	79	0.5	2.0	E
24/9/2012	Cloudy	27	88	105.0	6.0	E
25/9/2012	Sunny	27	82	20.5	8	E
26/9/2012	Cloudy	27	79	0.0	3.0	NE
28/9/2012	Sunny	29	53	0.0	9.0	NW
29/9/2012	Sunny	32	56	0.0	8.0	NW
30/9/2012	Sunny	27	61	0.0	8.0	NW

Date	Weather	Kai Tak Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	12	SE
4/9/2012	Sunny	27	86	17.5	15	E
6/9/2012	Sunny	29	81	2.5	9	NE
8/9/2012	Sunny	28	79	12.0	Not available	Not available
12/9/2012	Sunny	29	78	0.0	10.0	SE
14/9/2012	Sunny	26	63	0.0	12.0	NW
20/9/2012	Sunny	27	79	0.5	16.0	E
24/9/2012	Cloudy	32	88	105.0	6.0	SE
25/9/2012	Sunny	27	82	20.5	20.0	E
26/9/2012	Cloudy	29	79	0.0	5.0	E
28/9/2012	Sunny	31	53	0.0	18.0	N
29/9/2012	Sunny	31	56	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	9.7	N


Date	Weather	Green Island Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	15	NE
4/9/2012	Sunny	27	86	17.5	25	NE
6/9/2012	Sunny	29	81	2.5	30	NE
8/9/2012	Sunny	28	79	12.0	20	Not available
12/9/2012	Sunny	29	78	0.0	9	SE
14/9/2012	Sunny	26	63	0.0	30	N
20/9/2012	Sunny	27	79	0.5	27	NE
24/9/2012	Cloudy	32	88	105.0	8	S
25/9/2012	Sunny	27	82	20.5	35	NE
26/9/2012	Cloudy	29	79	0.0	12	SE
28/9/2012	Sunny	31	53	0.0	25	N
29/9/2012	Sunny	31	56	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	19	N

- \* King's Park's data
- Data were not available
- # less than 24 hourly observations per day






Normal Weekdays Noise Monitoring Results at NM2 ( $L_{eq, 30min}$ )

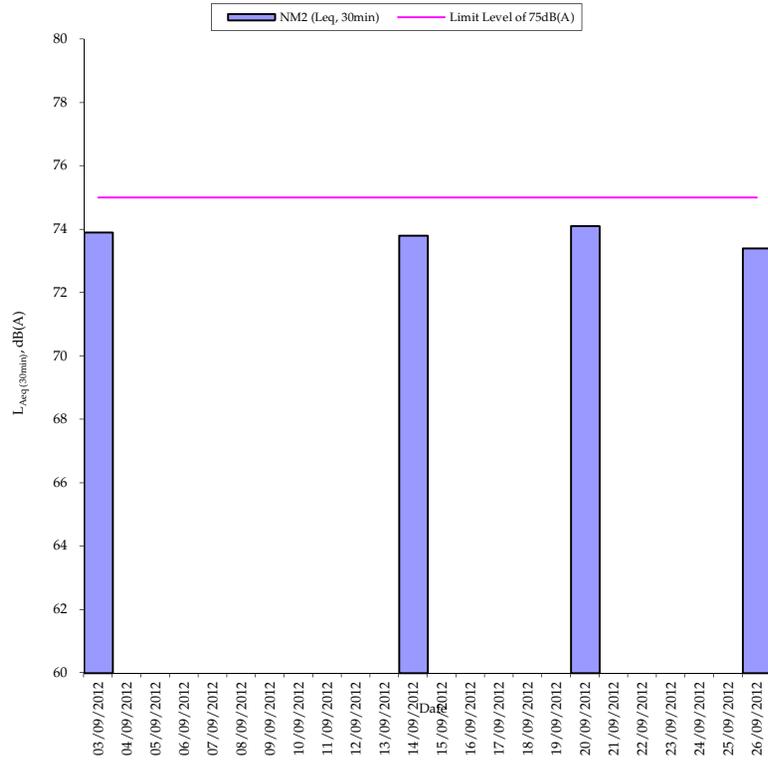

Remark:  
- 75dB(A) was adopted as the Limit Level during normal weekdays in the reporting period

Restricted Hours Noise Monitoring Results at NM2 ( $L_{eq, 5min}$ )

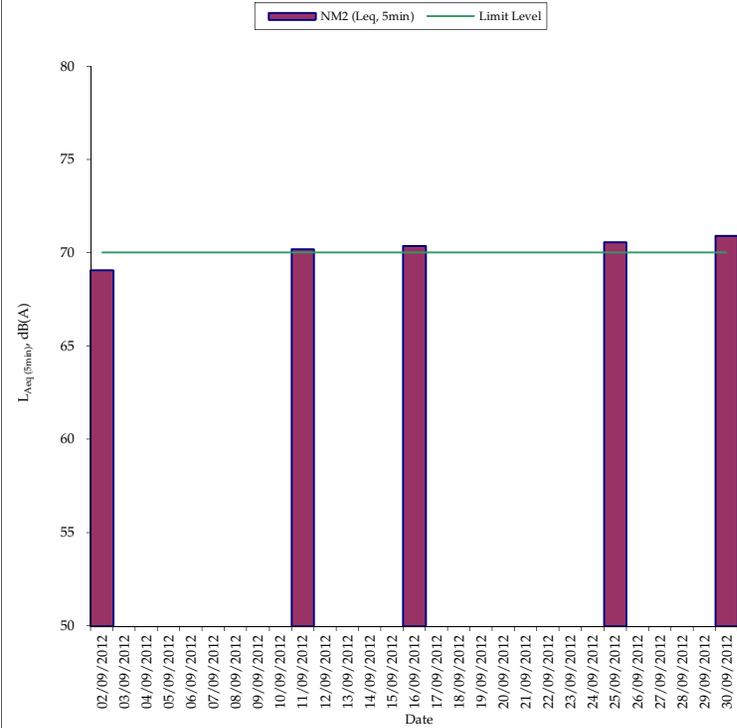

Remark:  
- 70dB(A) was adopted as the Limit Level during restricted hours in the reporting period  
- 55dB(A) was adopted as the Limit Level during night time period

*Annex D7 Cumulative Complaint and Summons/Prosecutions Log*

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
December 2009	0	0
January 2010	0	0
February 2010	0	0
March 2010	0	0
April 2010	0	0
May 2010	0	0
June 2010	0	0
July 2010	0	0
August 2010	0	0
September 2010	0	0
October 2010	0	0
November 2010	0	0
December 2010	0	0
January 2011	0	0
February 2011	0	0
March 2011	0	0
April 2011	0	0
May 2011	0	0

*Annex D7 Cumulative Complaint and Summons/Prosecutions Log*

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
June 2011	0	0
July 2011	0	0
August 2011	0	0
September 2011	0	0
October 2011	0	0
November 2011	1	0
December 2011	0	0
January 2012	0	0
February 2012	0	0
March 2012	0	0
April 2012	0	0
May 2012	0	0
June 2012	0	0
July 2012	0	0
August 2012	0	0
September 2012	0	0
Overall Total	1	0

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	% Comp	2010	2011	2012	2013	2014
<b>HATS Stage 2A - Contract DC/2007/23</b>										
<b>Central PTW Drop Shaft</b>										
<b>EBS, Env. &amp; Geotechnical Instrumentations</b>										
<b>Markers/UMP's/Others(Same note as Piez.)</b>										
CEDES0439	CEDES: Install SS Markers (70 Nos.)	50	21OCT09A	11FEB10	60					
CEDES0441	CEDES: JointSurvey&EstablishBaseline Readings SSM	14	12FEB10	03MAR10	0					
CEDES0445	CEDES: Consent Location and Permits	30	12FEB10	22MAR10	0					
CEDES0447	CEDES: Install UMP (3 Nos.) Additional	60	23MAR10	02JUN10	0					
CEDES0449	CEDES: EstablishBaseline Readings for UMP	14	03JUN10	19JUN10	0					
CEDES0454	CEDES: Review Comment&Approve by WHTCL	25	28NOV09A	23JAN10	84					
CEDES0456	CEDES: Instrumentation Installation @ WHT	60	25JAN10	08APR10	0					
CEDES0458	CEDES: Baseline Establishment @ WHT	28	09APR10	12MAY10	0					
<b>Piezometers(NearbyPTWorPScoversedinthisInstalln)</b>										
CEDES0397	CEDES: Installation Works of BH843 Piezometer	21	20JAN10	12FEB10	0					
CEDES0399	CEDES: BH843 Piezometer Baseline Establishment	26	13FEB10	18MAR10	0					
CEDES0401	CEDES: Excav.Permit/TTA/TTM ApplicationforBH946PW	24	25SEP09A	08FEB10	30					
CEDES0403	CEDES: Installation Works of BH946 Piezometer	21	13FEB10	12MAR10	0					
CEDES0405	CEDES: BH946 Piezometer Baseline Establishment	26	13MAR10	13APR10	0					
CEDES0407	CEDES: Excav.Permit/TTA/TTM ApplicationforBH846PW	24	28SEP09A	08FEB10	30					
CEDES0409	CEDES: Installation Works of BH846 Piezometer	21	09FEB10	08MAR10	0					
CEDES0411	CEDES: BH846 Piezometer Baseline Establishment	26	09MAR10	08APR10	0					
CEDES0415	CEDES: Installation Works of BH844 Piezometer	21	09MAR10	01APR10	0					
CEDES0417	CEDES: BH844 Piezometer Baseline Establishment	26	02APR10	04MAY10	0					
CEDES0419	CEDES: Excav.Permit/TTA/TTM ApplicationforBH847PW	24	28SEP09A	06FEB10	35					
CEDES0421	CEDES: Installation Works of BH847 Piezometer	21	02APR10	27APR10	0					
CEDES0423	CEDES: BH847 Piezometer Baseline Establishment	26	28APR10	28MAY10	0					
<b>Electrical &amp; Mechanical Installations</b>										
CEDES0600	CEDES: LV Application to HKEC	6	04FEB10*	10FEB10	0					
CEDES0605	CEDES: Installation Works for LV Application	60	11FEB10	26APR10	0					
CEDES0610	CEDES: LV Connection & Power On	4	27APR10	30APR10	0					
<b>Marine Dumping Permit</b>										
CEDES0390	CEDES: Request for Disposal Site&Get Permit	24	06JAN10A	02FEB10	50					
<b>Diaphragm Wall</b>										
CEDES0205C	CEDES: Pretrenching Stage 1	14	09JAN10A	22JAN10	79					
CEDES0205E	CEDES: Preboring by Casing Installation Stage 2	45	23JAN10	19MAR10	0					
CEDES0210	CEDES: Pre-Treatment of Ground	31	20JAN10	27FEB10	0					
CEDES0215	CEDES: Guide Wall Construction	12	06FEB10	23FEB10	0					
CEDES0220	CEDES: Set Up of Bentonite Yard	9	24FEB10	05MAR10	0					
CEDES0252	CEDES: Excavate 1st Panel to Formation Level	15	06MAR10	23MAR10	0					
CEDES0253	CEDES: 1st Panel Desanding & Preparation Works	4	24MAR10	27MAR10	0					
CEDES0254	CEDES: 1st Panel Rebar Cage Installation	6	29MAR10	03APR10	0					
CEDES0256	CEDES: 1st Panel Concreting Works	1	06APR10	06APR10	0					
CEDES0257	CEDES: Excavate 2nd Panel to Formation Level	12	07APR10	20APR10	0					
CEDES0259	CEDES: 2nd Panel Desanding & Preparation Works	3	21APR10	23APR10	0					
CEDES0261	CEDES: 2nd Panel Rebar Cage Installation	5	24APR10	29APR10	0					
CEDES0263	CEDES: 2nd Panel Concreting Works	1	30APR10	30APR10	0					
CEDES0265	CEDES: Excavate 3rd Panel to Formation Level	12	03MAY10	15MAY10	0					
CEDES0267	CEDES: 3rd Panel Desanding & Preparation Works	3	17MAY10	19MAY10	0					
CEDES0269	CEDES: 3rd Panel Rebar Cage Installation	5	20MAY10	25MAY10	0					
CEDES0271	CEDES: 3rd Panel Concreting Works	1	26MAY10	26MAY10	0					
CEDES0273	CEDES: Excavate 4th Panel to Formation Level	12	27MAY10	09JUN10	0					
CEDES0274	CEDES: Grouting Works Phase 1	51	04JUN10	04AUG10	0					
CEDES0275	CEDES: 4th Panel Desanding & Preparation Works	3	10JUN10	12JUN10	0					
CEDES0277	CEDES: 4th Panel Rebar Cage Installation	5	14JUN10	19JUN10	0					
CEDES0279	CEDES: 4th Panel Concreting Works	1	21JUN10	21JUN10	0					
CEDES0281	CEDES: Excavate 5th Panel to Formation Level	12	22JUN10	06JUL10	0					
CEDES0283	CEDES: 5th Panel Desanding & Preparation Works	3	07JUL10	09JUL10	0					
CEDES0285	CEDES: 5th Panel Rebar Cage Installation	5	10JUL10	15JUL10	0					
CEDES0287	CEDES: 5th Panel Concreting Works	1	16JUL10	16JUL10	0					
CEDES0289	CEDES: Excavate 6th Panel to Formation Level	12	17JUL10	30JUL10	0					
CEDES0291	CEDES: 6th Panel Desanding & Preparation Works	3	31JUL10	03AUG10	0					
CEDES0292	CEDES: Grouting Works Phase 2	34	05AUG10	13SEP10	0					
CEDES0293	CEDES: 6th Panel Rebar Cage Installation	5	04AUG10	09AUG10	0					
CEDES0295	CEDES: 6th Panel Concreting Works	1	10AUG10	10AUG10	0					
CEDES0297	CEDES: Excavate 7th Panel to Formation Level	12	11AUG10	24AUG10	0					
CEDES0299	CEDES: 7th Panel Desanding & Preparation Works	3	25AUG10	27AUG10	0					
CEDES0301	CEDES: 7th Panel Rebar Cage Installation	5	28AUG10	02SEP10	0					
CEDES0303	CEDES: 7th Panel Concreting Works	1	03SEP10	03SEP10	0					
CEDES0305	CEDES: Install Temp Steel Casing	28	14SEP10	19OCT10	0					
CEDES0306	CEDES: Grouting for Temp Casing	19	20OCT10	10NOV10	0					
CEDES0307	CEDES: Install Dewatering Wells for Pump-test	12	02NOV10	15NOV10	0					
CEDES0310	CEDES: Pumping Test	6	16NOV10	22NOV10	0					
CEDES0320	CEDES: Submission of Pumping Test Report	6	23NOV10	29NOV10	0					
CEDES0330	CEDES: Demobilization for D'wall	6	23NOV10	29NOV10	0					
<b>Shaft Excavation</b>										
CEDES0400	CDS: Construct Capping Beam & Shaft Collar	12	22NOV10	04DEC10	0					
CEDES0410	CDS: Excavate Soil & Ring Beams (24.93m)	11	06DEC10	17DEC10	0					
CEDES0420	CDS: Construct Levelling Pad	6	18DEC10	24DEC10	0					
CEDES0430	CDS: Pre-excavation Grout for Raise Bore	90	27DEC10	15APR11	0					
CEDES0440	CDS: In-fill Concrete for Pilot Hole	12	16APR11	29APR11	0					
CEDES1580	CDS: Compl Excav. to Rockhead at CTL DS(KD-C)	0		17DEC10	0					
CEDES1590	CDS: Compl D'wall, Soil Excav&Clear Area(KD-03)	0		17DEC10	0					
<b>Raised Boring</b>										
CEDES0700	CDS: Rig Up Hole 1	5	03APR12	09APR12	0					
CEDES0710	CDS: Pilot Drill 100 mtrs	14	10APR12	25APR12	0					
CEDES0720	CDS: Attach reamer and Collar	3	26APR12	28APR12	0					
CEDES0730	CDS: Ream 100 metres @ 2.8 mtr dia	27	30APR12	31MAY12	0					
CEDES0740	CDS: Lower Reamer and Remove	3	01JUN12	04JUN12	0					

Start Date	31JUL09	Early Bar	WPU7	Sheet 1 of 2		Date	Revision	Checked/Approved
Finish Date	15JAN15	Progress Bar	<b>Labour Area Treatment Scheme Stage 2A</b> <b>Contract No. DC/2007/23 - Construction of Sewage</b> <b>Conveyance from North Point to Stonecutters Island</b> <b>Programme</b>					
Data Date	20JAN10	Critical Activity	<b>Annex E8 Construction Programme for the Project</b>					
Run Date	01FEB10 09:59							

© Primavera Systems, Inc.








Annex E

## Central Drop Shaft

**Key**

-  Shaft Excavation Location
-  Site Location

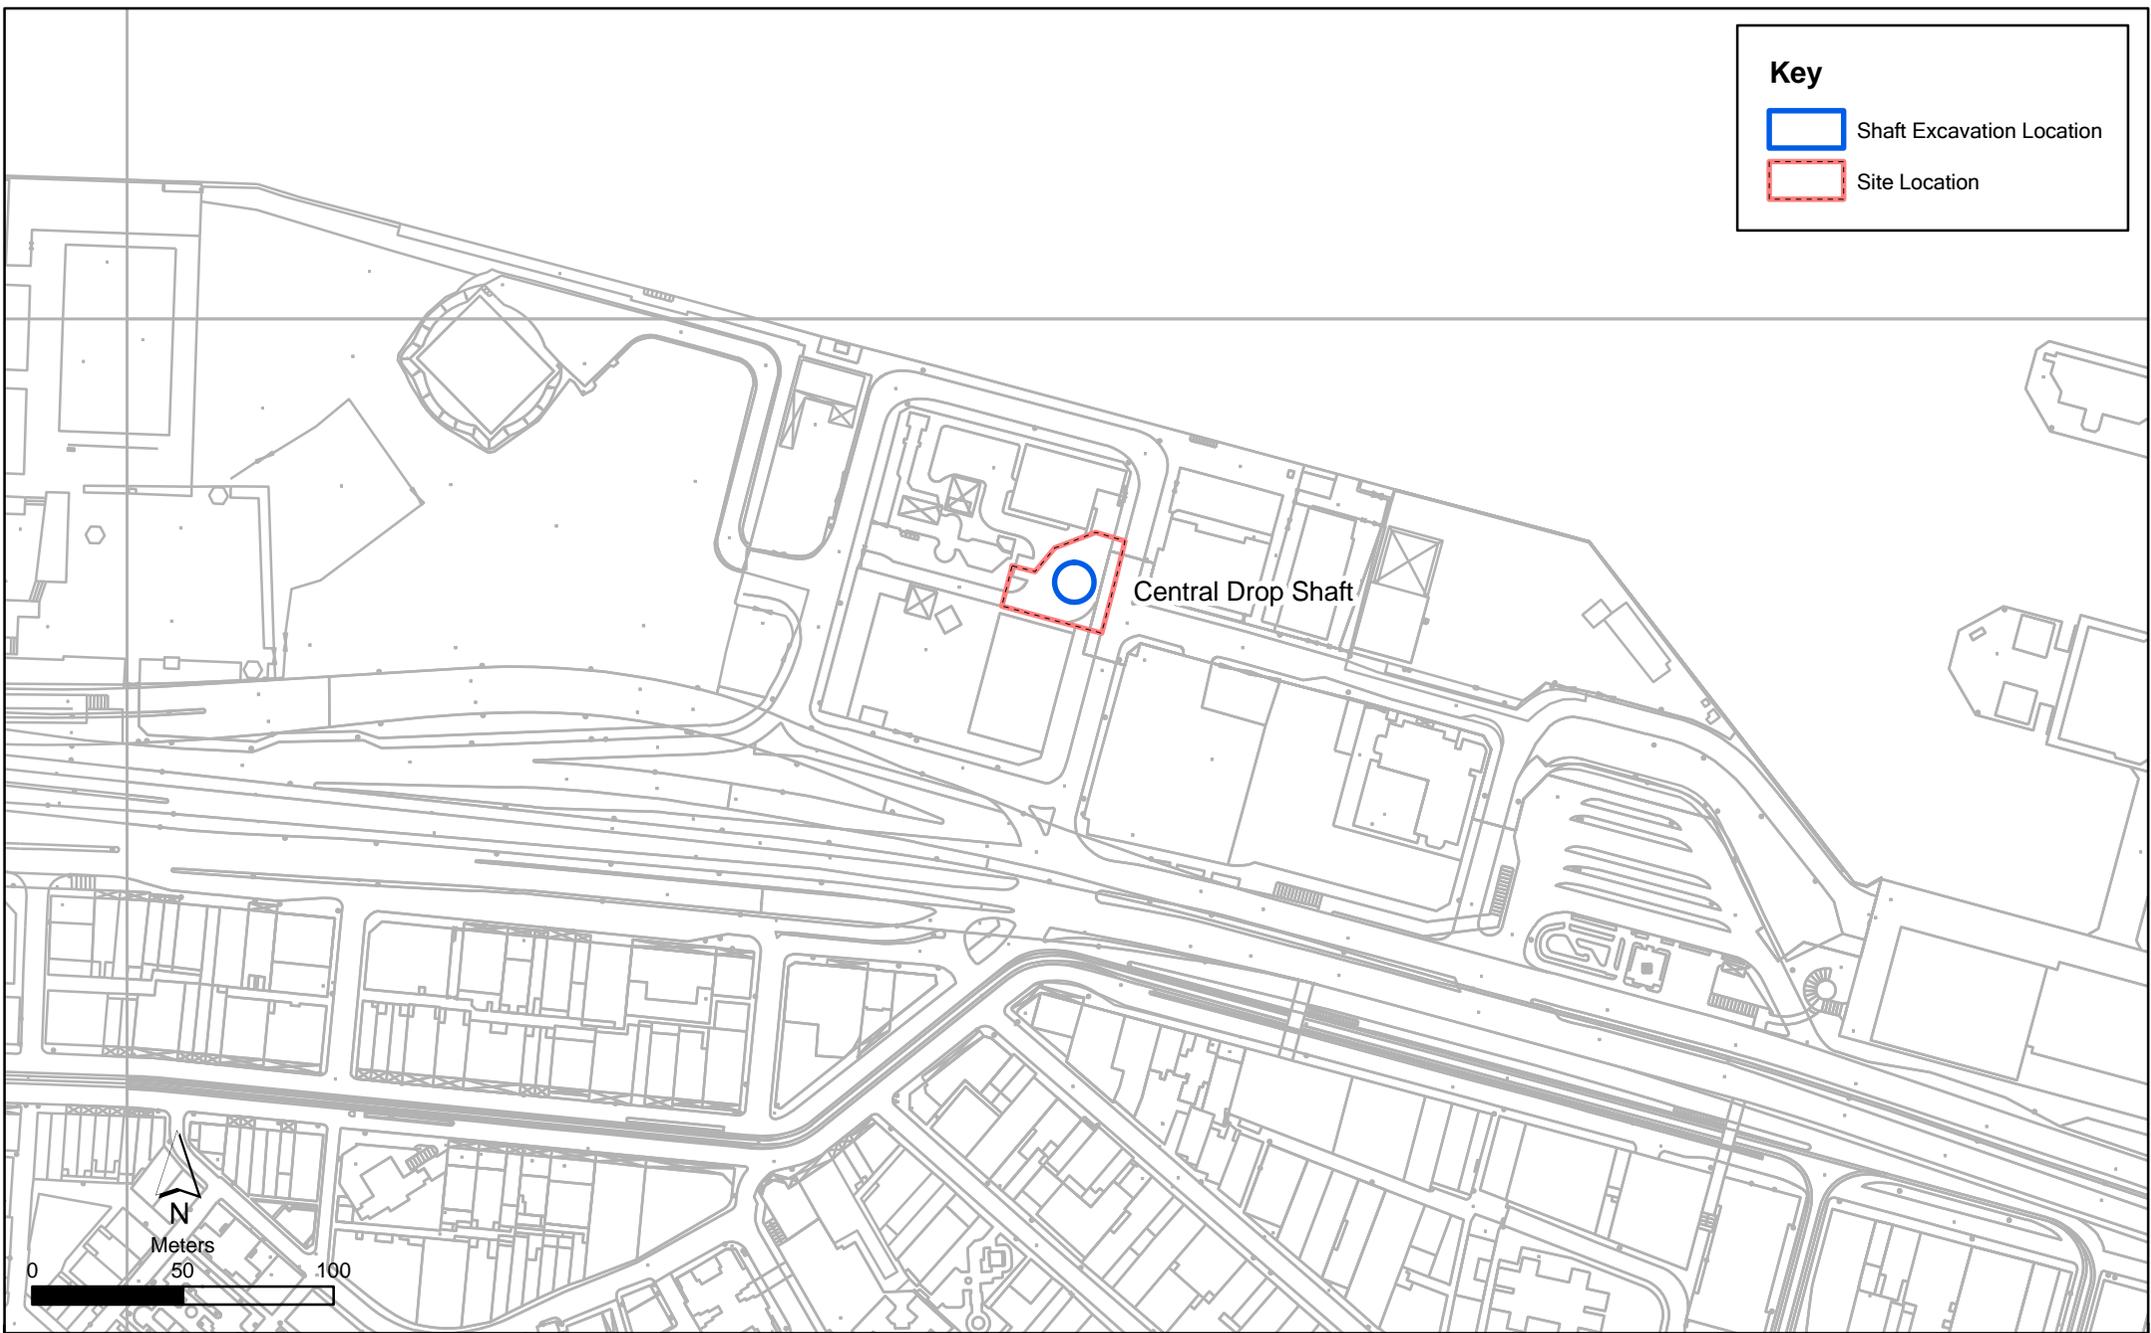

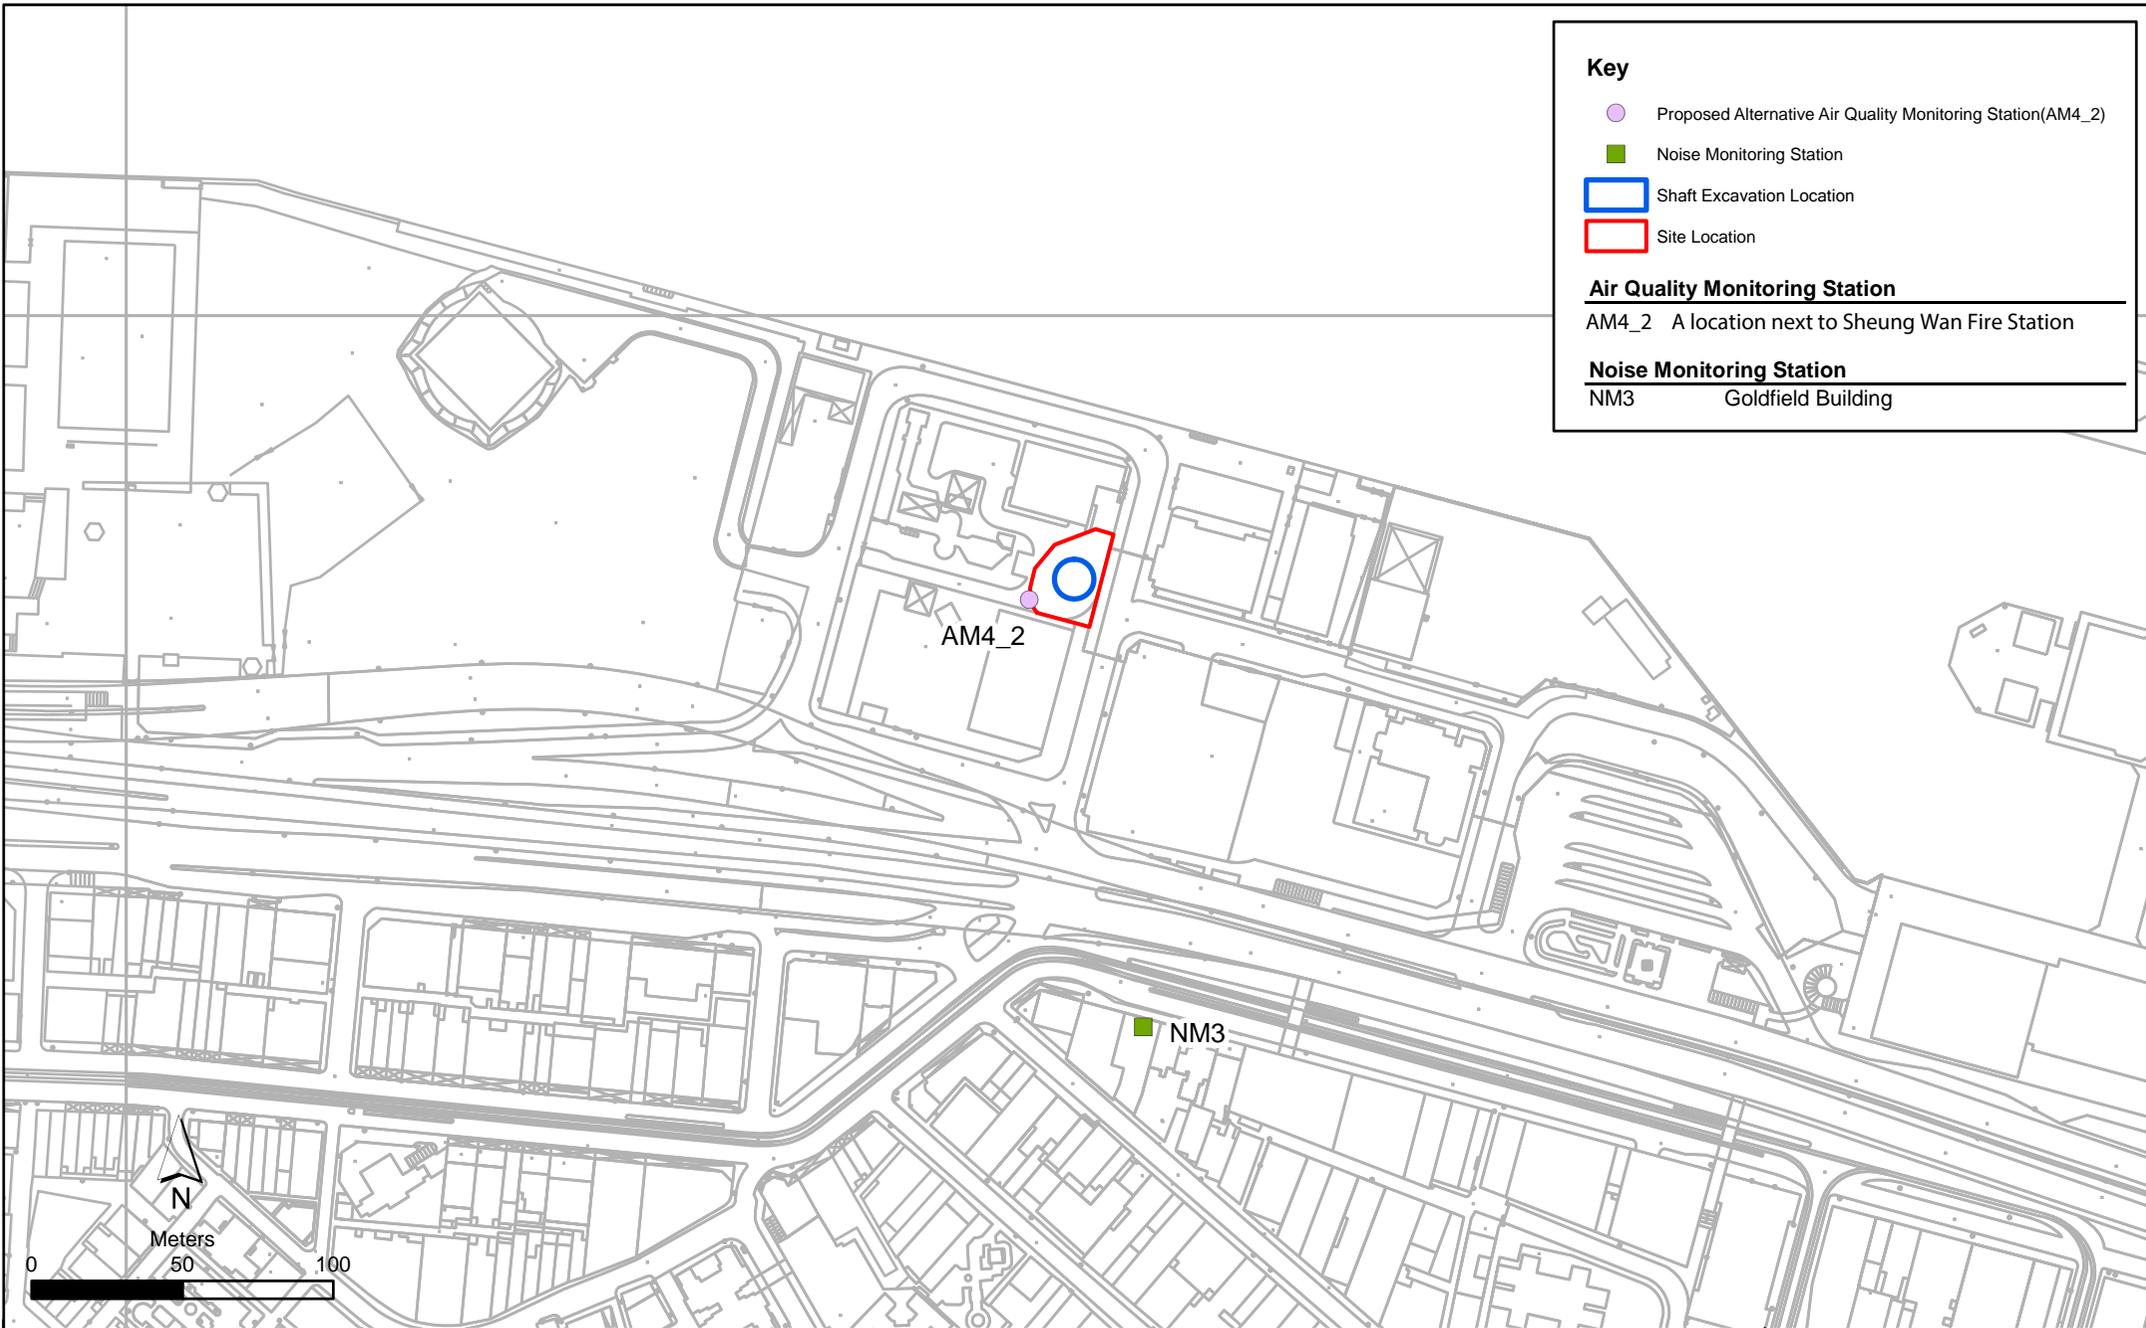

**Key**

- Proposed Alternative Air Quality Monitoring Station (AM4\_2)
- Noise Monitoring Station
- Shaft Excavation Location
- Site Location

---

**Air Quality Monitoring Station**

AM4\_2 A location next to Sheung Wan Fire Station

---

**Noise Monitoring Station**

NM3 Goldfield Building

Annex E2

Contract No. DC/2007/23  
 Harbour Area Treatment Scheme Stage 2A  
 Construction of Sewage Conveyance System from North Point to Stonecutters Island  
*Impact Air Quality & Noise Monitoring Stations (Central)*

**Environmental  
Resources  
Management**



File: EM&A and proposed stations\  
 0104887\_Centra\_NMAM\_Annex\_Oct2012.mxd  
 Date: 10-Oct-12

## Annex E3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23

Harbour Area Treatment Scheme Stage 2A

Construction of Sewage Conveyance System from North Point to Stonecutters Island

Impact Construction Air Quality Monitoring Schedule

**AM4\_2 - A Location within the DSD Central PTW**

**Monitoring Month : September 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
	1-hr and 24-hr Monitoring					1-hr and 24-hr Monitoring
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
					1-hr and 24-hr Monitoring	
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
				1-hr and 24-hr Monitoring		
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
			1-hr and 24-hr Monitoring			1-hr and 24-hr Monitoring
30-Sep						

**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
	Public Holiday	Public Holiday			1-hr and 24-hr Monitoring	
7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
				1-hr and 24-hr Monitoring		
14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
			1-hr and 24-hr Monitoring			
21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct
	1-hr and 24-hr Monitoring	Public Holiday				1-hr and 24-hr Monitoring
28-Oct	29-Oct	30-Oct	31-Oct			

# Annex E3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23  
 Harbour Area Treatment Scheme Stage 2A  
 Construction of Sewage Conveyance System from North Point to Stonecutters Island  
 Impact Construction Noise Quality Monitoring Schedule

NM3 - Goldfield Building  
 Monitoring Month : September 2012

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
	Noise Monitoring					
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
					Noise Monitoring	
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
				Noise Monitoring		
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
			Noise Monitoring			
30-Sep						

**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct	7-Oct
	Public Holiday	Public Holiday			Noise Monitoring	
8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct	14-Oct
				Noise Monitoring		
15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct	21-Oct
			Noise Monitoring			
22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct	28-Oct
	Noise Monitoring	Noise Monitoring (Evening time) Public Holiday				
29-Oct	30-Oct	31-Oct				

**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Construction Phase</i>			
Air Quality	<p>The Air Pollution Control (Construction Dust) Regulation shall be implemented and good site practices shall be incorporated in the contract clauses to minimize construction dust impact. Control measures relevant to this Project are listed below:</p> <ul style="list-style-type: none"> <li>• skip hoist for material transport should be totally enclosed by impervious sheeting;</li> <li>• every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site;</li> <li>• the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;</li> <li>• where a site boundary adjoins a road, streets or other accessible to the public, hoarding of not less than 2.4 m high from ground level should be provided along the entire length except for a site entrance or exit;</li> <li>• every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the 3 sides;</li> <li>• regular watering, with complete coverage, to reduce dust emission from exposed site surfaces and unpaved roads, particularly during dry weather;</li> <li>• site enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines;</li> <li>• open stock piles should be avoided or covered and prevent placing dusty material storage piles near ASRs if possible;</li> <li>• tarpaulin covering of all dusty vehicle loads transported to, from and between site locations; and</li> <li>• instigation of an environmental monitoring auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.</li> </ul>	All work sites / during construction	√
Air Quality	<p>The following watering measures for specific site would be required to control the fugitive dust impacts:</p> <ul style="list-style-type: none"> <li>• watering four times per day within worksites at the Central PTW.</li> </ul>	All work sites / during construction	√
<i>Operational Phase</i>			



**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Air Quality	<p>Good housekeeping for SCISTW and PTWs listed below should be followed to ameliorate any odour impact from the plant and these standard practices should be included in the plant operator manual.</p> <ul style="list-style-type: none"> <li>• Screens should be cleaned regularly to remove any accumulated organic debris</li> <li>• Grit and screening transfer systems should be flushed regularly with water to remove organic debris and grit</li> <li>• Grit and screened materials should be transferred to closed containers to minimize odour escape</li> <li>• Scum and grease collection wells and troughs should be emptied and flushed regularly to prevent putrefaction of accumulated organics</li> <li>• Skim and remove floating solids and grease from primary clarifiers regularly</li> <li>• Frequent sludge withdrawal from tanks is necessary to prevent the production of gases</li> <li>• Sludge cake should be transferred to closed containers</li> <li>• Sludge containers should be flushed with water regularly</li> </ul>	All work sites / during construction	NA. Measures not required until commencement of operational phase
Air Quality	Commissioning tests for all deodorization system should be included in the Design and Construction Contract Document.	All PTW and SCISTW/ during operational phase	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			
Noise	Use of quiet PME, movable barriers and acoustic mats	All work sites / during construction	√

**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Noise	<p>Good Site Practice:</p> <ul style="list-style-type: none"> <li>• only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program;</li> <li>• silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program;</li> <li>• mobile plant, if any, should be sited as far from NSRs as possible;</li> <li>• machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;</li> <li>• plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>• material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities;</li> </ul> <p>Environmental audit shall be carried out to ensure that appropriate noise control measures would be properly implemented.</p>	All work sites / during construction	√
<i>Construction Phase</i>			
Water Quality	<p>Construction Site Runoff and General Construction Activities</p> <p>The mitigation measures as outlined in the ProPECC PN 1/94 Construction Site Drainage should be adopted where applicable.</p>	All work sites / during construction	√

**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Effluent Discharge</p> <p>There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD. Minimum distances of 100 m should be maintained between the discharge points of construction site effluent and the existing saltwater intakes.</p>	All work sites / during construction	√
Water Quality	<p>Accidental Spillage of Chemicals</p> <p>Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.</p>	All work sites / during construction	√
Water Quality	<p>Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.</p>	All work sites / during construction	√

**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes.</p> <p>General requirements are given as follows:</p> <ul style="list-style-type: none"> <li>• Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</li> <li>• Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents.</li> <li>• Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.</li> </ul>	All work sites / during construction	√

**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Construction Works in Close Proximity of Storm Drains or Seafront</p> <p>To minimize the potential water quality impacts from the construction works located at or near any watercourse, the practices outlined below should be adopted where applicable.</p> <ul style="list-style-type: none"> <li>• The use of less or smaller construction plants may be specified to reduce the disturbance to the storm water courses or marine environment.</li> <li>• Temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works.</li> <li>• Stockpiling of construction materials and dusty materials should be covered and located away from any water courses.</li> <li>• Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers.</li> <li>• Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the waterfront, where practicable.</li> <li>• Proper shoring may need to be erected in order to prevent soil/mud from slipping into the storm culvert or sea</li> </ul>	All work sites / during construction	√

**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Operational Phase</i>			
Water Quality	Dual power supply, standby facilities for the main treatment units and standby equipment parts / accessories should be provided as far as possible at the SCISTW to minimize the chance of emergency discharge.	SCISTW and all the Stage 2 PTWs / Operation Stage	NA. Measures not required until commencement of operational phase
Water Quality	Standby unit(s) and dual (backup) power supply would be provided at all the Stage 2 PTWs to reduce the risk of equipment breakdown at the PTWs.	Stage 2 PTWs / Operation Stage	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			
Waste	Reusable steel or concrete panel shutters, fencing and hoarding and signboard should be used as a preferred alternative to items made of wood, to minimise wastage of wood. Attention should be paid to WBTC No. 19/2001 - Metallic Site Hoardings and Signboards to reduce the amount of timber used on construction sites. Metallic alternatives to timber are readily available and should be used rather than new timber. Precast concrete units should be adopted wherever feasible to minimize the use of timber formwork.	All work sites / during the construction period	√
Waste	All waste materials should be segregated into categories covering: <ul style="list-style-type: none"> <li>• excavated materials suitable for reuse on-site;</li> <li>• excavated materials suitable for public filling facilities;</li> <li>• remaining C&amp;D waste for landfill;</li> <li>• chemical waste; and</li> <li>• general refuse for landfill.</li> </ul>	All work sites / during the construction period	√

**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	<p>Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> <li>• Sort C&amp;D waste from demolition of existing facilities to recover recyclable portions such as metals;</li> <li>• Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>• Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force;</li> <li>• Any unused chemicals or those with remaining functional capacity shall be recycled; and</li> <li>• Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> </ul>	All work sites / during the construction period	√
Waste	<p>Recommendations for good site practices during construction activities include:-</p> <ul style="list-style-type: none"> <li>• Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site</li> <li>• Training of site personnel in proper waste management and chemical waste handling procedures</li> <li>• Develop and provide toolbox talk for on-site sorting of C&amp;D materials to enhance worker’s awareness in handling, sorting, reuse and recycling of C&amp;D materials.</li> <li>• Provision of sufficient waste disposal points and regular collection of waste</li> <li>• Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors</li> </ul>	All work sites / during the construction period	√
Waste	<p>Bentonite slurries used in diaphragm wall construction should be reconditioned and reused wherever practicable. The disposal of residual used bentonite slurry should follow the good practice guidelines stated in ProPECC PN 1/94 “Construction Site Drainage”.</p>	All work sites / during the construction period	√

**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	Adequate number of portable toilets at temporary works areas or the PTWs to ensure that sewage from site staff would be properly collected.	All work sites / during the construction period	√
Waste	General refuse should be stored in enclosed bins, skips or compaction units separating from C&D material and disposed of at designated landfill.	All work sites / during the construction period	√
Waste	The recyclable component of the municipal waste generated by the workforce, such as aluminium cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.	All work sites / during the construction period	√
Waste	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the approved Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	All work sites / during the construction period	√



**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	Prior to excavation of the marine deposit layer, the deposit should be tested in accordance with the ETWB TC(W) No. 34/2002 and the results should be presented in a Preliminary Sediment Quality Report. The marine deposit should be disposed of at the disposal site designated by the Marine Fill Committee (MFC) or Director of Environmental Protection (DEP) depending on the test results.	All work sites / during the construction period	√
<i>Construction Phase</i>			
Landscape & Visual	<ul style="list-style-type: none"> <li>• Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.</li> <li>• Existing trees to be retained on site should be carefully protected during construction.</li> <li>• Trees unavoidably affected by the works should be transplanted where practical.</li> <li>• Compensatory tree planting should be provided to compensate for felled trees.</li> <li>• Control of night-time lighting.</li> <li>• Erection of decorative screen hoarding compatible with the surrounding setting.</li> </ul>	All the works areas, PTWs and SCISTW / during the construction period	√
<i>Operational Phase</i>			
Landscape & Visual	<ul style="list-style-type: none"> <li>• Aesthetic design of the façade of PTW and associated structures to harmonize with the surrounding settings.</li> <li>• Shrub and Climbing Plants to soften proposed structures / Roof Greening.</li> <li>• Buffer Tree and Shrub Planting to screen proposed associated structures.</li> <li>• Reinstated of disturbed area</li> </ul>	All the works areas, PTWs and SCISTW / during the construction period	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			

**ANNEX E4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Cultural Heritage	The construction vibration control limit (ppv of 25mm/s) shall be strictly followed.	Identified historical buildings/ structures as mentioned in Tables 15.8 and 15.9. During blasting for tunnel, shafts, effluent conveyance system and disinfection facilities in the vicinity of the buildings/ structures	NA. Vibration monitoring has not been launched during the reporting period.
	Monitoring of vibration limits shall be conducted and reported as a requirement of EM&A programme	Identified historical buildings/ structures as mentioned in Tables 15.8 and 15.9. During blasting for tunnel, shafts, effluent conveyance system and disinfection facilities in the vicinity of the buildings/ structures	NA. Vibration monitoring has not been launched during the reporting period.

Remark:

- √ Compliance of Mitigation Measures
- <> Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Limited
- NA Not Applicable

## Annex E5 24-hour and 1-hour TSP Monitoring Results

### 1-hour TSP Monitoring Results

#### Station AM4\_2

Date	Start Time	Finish Time	Weather	TSP Concentration ( $\mu\text{g}/\text{m}^3$ )	Action Level ( $\mu\text{g}/\text{m}^3$ )	Limit Level ( $\mu\text{g}/\text{m}^3$ )	Site Conditions / Observations / Remarks	Temperature ( $^{\circ}\text{C}$ )	Wind Speed * (m/s)	Sampler ID	Filter ID
3-Sep-12	8:00	9:00	Sunny	98	393	500	Construction work in progress	32.8	<5	9315	1599
	9:02	10:02	Sunny	128	393	500	Construction work in progress	32.8	<5	9315	1600
	10:04	11:04	Sunny	117	393	500	Construction work in progress	32.8	<5	9315	1601
8-Sep-12	8:00	9:00	Sunny	156	393	500	Construction work in progress	30	<5	9315	1603
	9:02	10:02	Sunny	124	393	500	Construction work in progress	30	<5	9315	1605
	10:04	11:04	Sunny	122	393	500	Construction work in progress	30	<5	9315	1607
14-Sep-12	8:00	9:00	Sunny	133	393	500	Construction work in progress	29	<5	9315	1606
	9:02	10:02	Sunny	179	393	500	Construction work in progress	29	<5	9315	1608
	10:08	11:08	Sunny	129	393	500	Construction work in progress	29	<5	9315	1609
20-Sep-12	8:00	9:00	Cloudy	128	393	500	Construction work in progress	29	<5	9315	1607
	9:02	10:02	Cloudy	129	393	500	Construction work in progress	29	<5	9315	1632
	10:05	11:05	Cloudy	122	393	500	Construction work in progress	29	<5	9315	1634
26-Sep-12	11:12	12:12	Cloudy	122	393	500	Construction work in progress	30	<5	9315	1635
	12:52	13:52	Cloudy	164	393	500	Construction work in progress	30	<5	9315	1636
	13:54	14:54	Cloudy	183	393	500	Construction work in progress	30	<5	9315	1638
29-Sep-12	8:00	9:00	Sunny	105	393	500	Construction work in progress	29	<5	9315	1639
	9:02	10:02	Sunny	142	393	500	Construction work in progress	29	<5	9315	1651
	10:04	11:04	Sunny	120	393	500	Construction work in progress	29	<5	9315	1652
			<b>Min.</b>	<b>98</b>							
			<b>Max.</b>	<b>183</b>							
			<b>Average</b>	<b>133</b>							

\* Wind Speed data is presented in the Meteorological Data table


## Annex E5 24-hour and 1-hour TSP Monitoring Results

### 24-hour TSP Monitoring Results


#### Station AM4\_2

Start		Finish		Weather	Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m <sup>3</sup> /min)			TSP Conc. (µg/m <sup>3</sup> )	Action Level (µg/m <sup>3</sup> )	Limit Level (µg/m <sup>3</sup> )	Observations / Remarks	Sampler ID	Filter ID
Date	Time	Date	Time		Initial	Final	Initial	Final		Initial	Final	Average						
3-Sep-12	11:10	4-Sep-12	11:10	Sunny	2.8134	2.9500	14987.85	15011.85	24.00	1.24	1.24	1.24	77	211	260	Construction work in progress	9315	1602
8-Sep-12	11:06	9-Sep-12	11:06	Sunny	2.8279	2.9458	14990.85	15014.85	24.00	1.24	1.24	1.24	66	211	260	Construction work in progress	9315	1604
14-Sep-12	11:10	15-Sep-12	11:10	Sunny	2.8484	2.9797	15041.85	15065.85	24.00	1.24	1.24	1.24	74	211	260	Construction work in progress	9315	1633
20-Sep-12	11:12	21-Sep-12	11:12	Cloudy	2.8484	2.9801	15068.85	15092.85	24.00	1.22	1.22	1.22	75	211	260	Construction work in progress	9315	1631
26-Sep-12	15:00	27-Sep-12	15:00	Cloudy	2.8382	2.9649	15095.85	15119.85	24.00	1.22	1.22	1.22	72	211	260	Construction work in progress	9315	1637
29-Sep-12	11:06	30-Sep-12	11:06	Sunny	2.8385	2.9700	15122.85	15146.85	24.00	1.22	1.22	1.22	75	211	260	Construction work in progress	9315	1640
													Min.	66				
													Max.	77				
													Average	73				

**1-hr TSP Levels**  
**AM4\_2 (A location next to Sheung Wan Fire Station )**

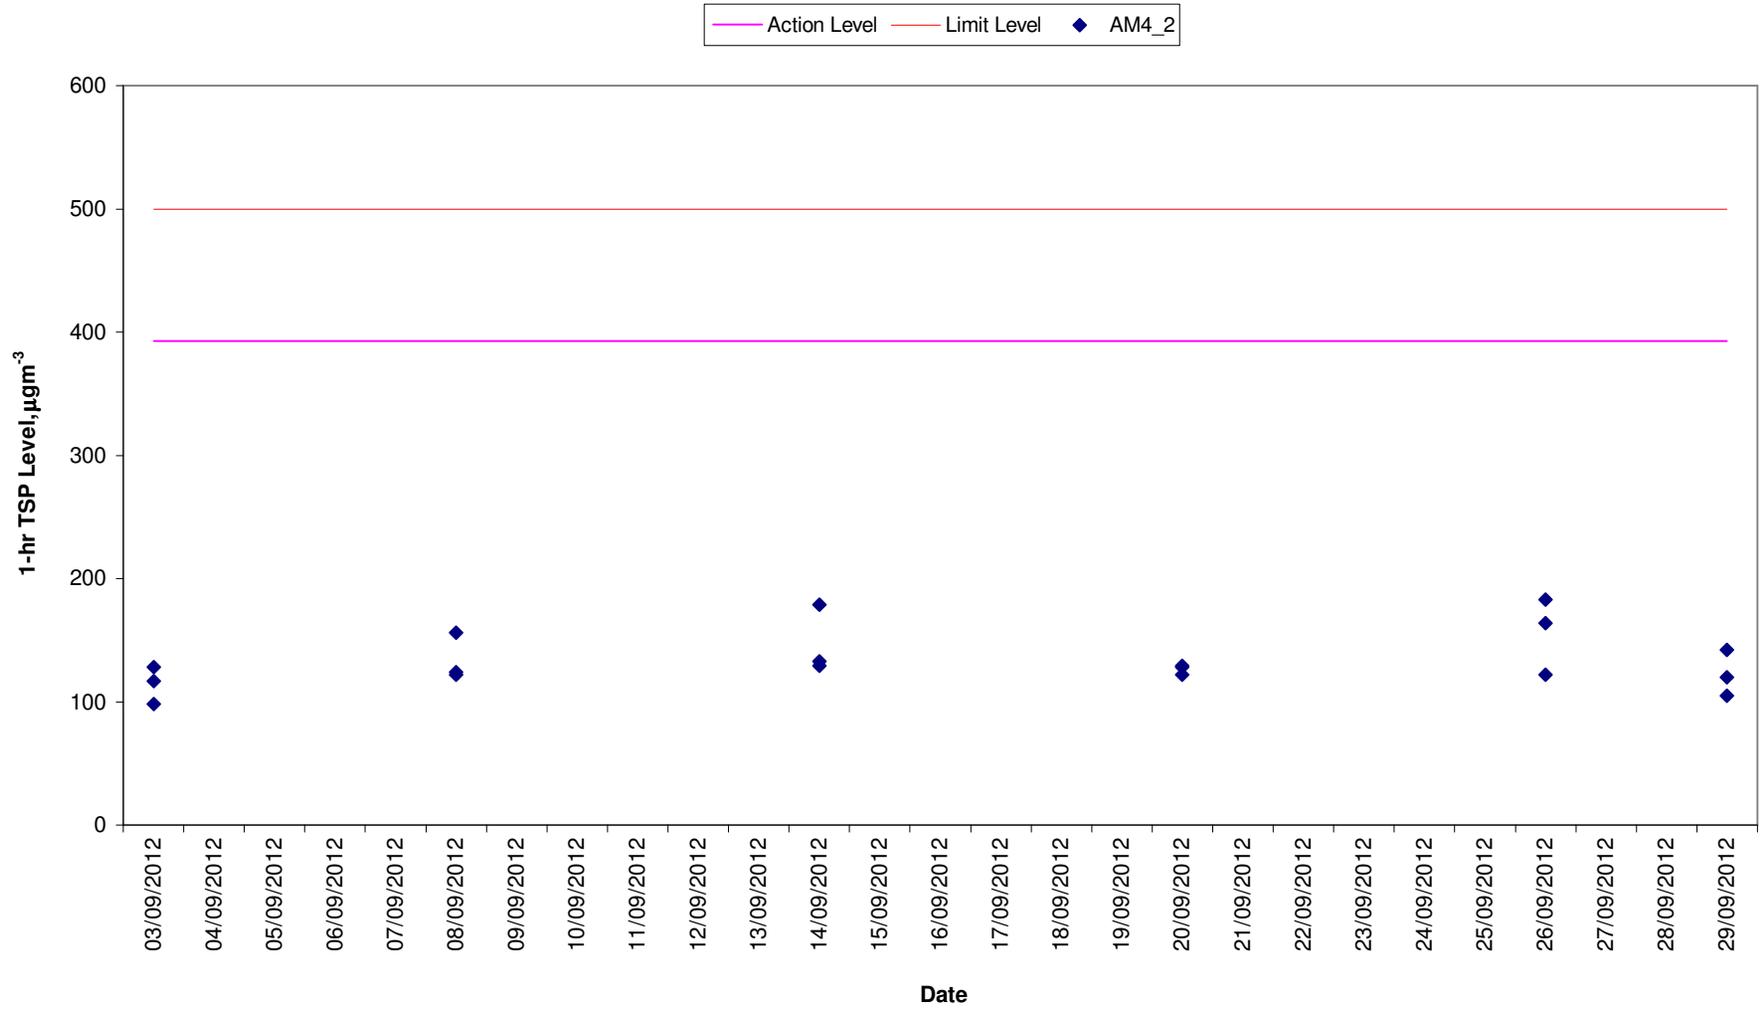

**24-hr TSP Levels**  
**AM4\_2 (A location next to Sheung Wan Fire Station)**

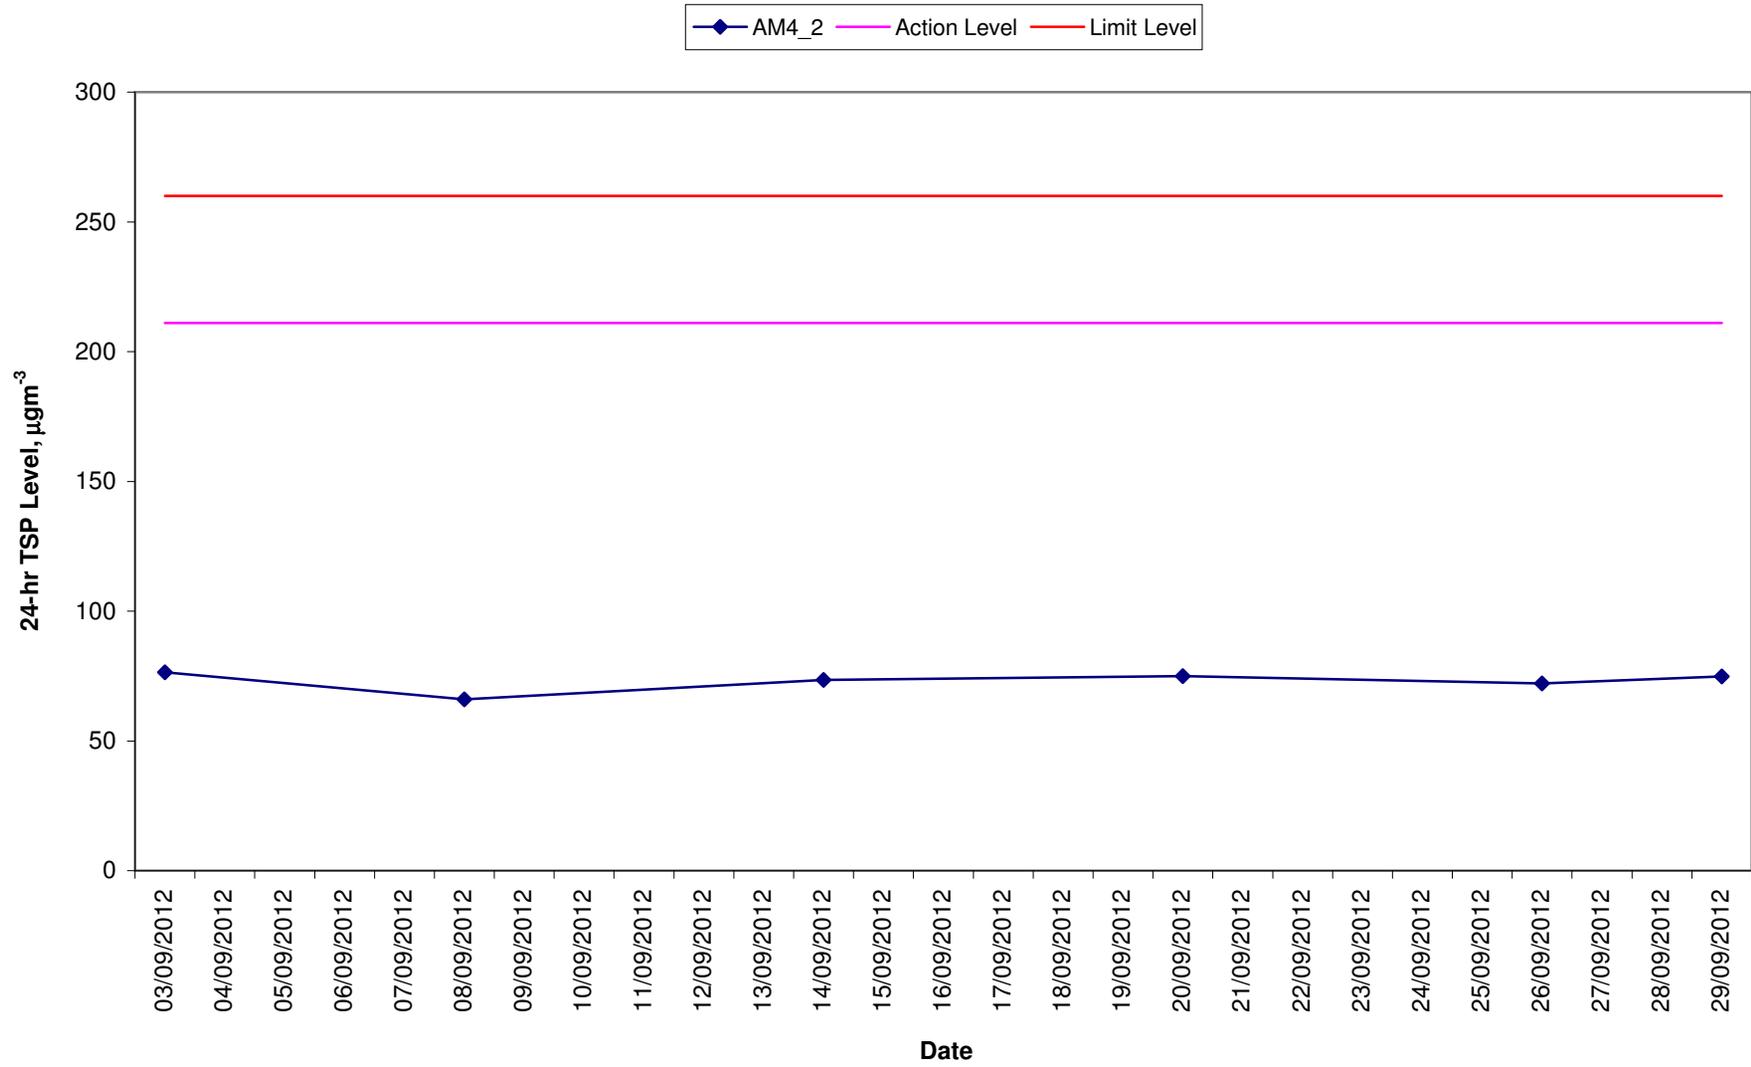

Meteorological Data Extracted from the Hong Kong Observatory

Date	Weather	King's Park Station				
		Average Air Temperature (°C)	Average Relative Humidity (%)	Total Rainfall (mm)	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	5	SE
4/9/2012	Sunny	27	86	17.5	7	E
6/9/2012	Sunny	29	81	2.5	8	E
8/9/2012	Sunny	28.4	79.0	12.0	Not available	Not available
12/9/2012	Sunny	29	78	0.0	9.0	SE
14/9/2012	Sunny	26	63	0.0	9.0	NE
20/9/2012	Sunny	27	79	0.5	Maintenance	E
24/9/2012	Cloudy	32	88	105.0	Maintenance	SE
25/9/2012	Sunny	27	82	20.5	Maintenance	Maintenance
26/9/2012	Cloudy	29	79	0.0	Maintenance	Maintenance
28/9/2012	Sunny	31	53	0.0	18.0	NE
29/9/2012	Sunny	30.8	56.0	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	8.3	N

Date	Weather	Tsing Yi Station				
		Average Air Temperature (°C)	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	27	77	0.0	10	E
4/9/2012	Sunny	28	86	17.5	9	E
6/9/2012	Sunny	30	81	2.5	5	SE
8/9/2012	Sunny	26	79	12.0	Not available	Not available
12/9/2012	Sunny	30	78	0.0	15.0	NE
14/9/2012	Sunny	27	63	0.0	9.0	NW
20/9/2012	Sunny	28	79	0.5	2.0	E
24/9/2012	Cloudy	27	88	105.0	6.0	E
25/9/2012	Sunny	27	82	20.5	8	E
26/9/2012	Cloudy	27	79	0.0	3.0	NE
28/9/2012	Sunny	29	53	0.0	9.0	NW
29/9/2012	Sunny	32	56	0.0	8.0	NW
30/9/2012	Sunny	27	61	0.0	8.0	NW

Date	Weather	Kai Tak Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	12	SE
4/9/2012	Sunny	27	86	17.5	15	E
6/9/2012	Sunny	29	81	2.5	9	NE
8/9/2012	Sunny	28	79	12.0	Not available	Not available
12/9/2012	Sunny	29	78	0.0	10.0	SE
14/9/2012	Sunny	26	63	0.0	12.0	NW
20/9/2012	Sunny	27	79	0.5	16.0	E
24/9/2012	Cloudy	32	88	105.0	6.0	SE
25/9/2012	Sunny	27	82	20.5	20.0	E
26/9/2012	Cloudy	29	79	0.0	5.0	E
28/9/2012	Sunny	31	53	0.0	18.0	N
29/9/2012	Sunny	31	56	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	9.7	N


Date	Weather	Green Island Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	15	NE
4/9/2012	Sunny	27	86	17.5	25	NE
6/9/2012	Sunny	29	81	2.5	30	NE
8/9/2012	Sunny	28	79	12.0	20	Not available
12/9/2012	Sunny	29	78	0.0	9	SE
14/9/2012	Sunny	26	63	0.0	30	N
20/9/2012	Sunny	27	79	0.5	27	NE
24/9/2012	Cloudy	32	88	105.0	8	S
25/9/2012	Sunny	27	82	20.5	35	NE
26/9/2012	Cloudy	29	79	0.0	12	SE
28/9/2012	Sunny	31	53	0.0	25	N
29/9/2012	Sunny	31	56	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	19	N

- \* King's Park's data
- Data were not available
- # less than 24 hourly observations per day





Normal Weekdays Noise Monitoring Results at NM3 ( $L_{Aeq, 30min}$ )

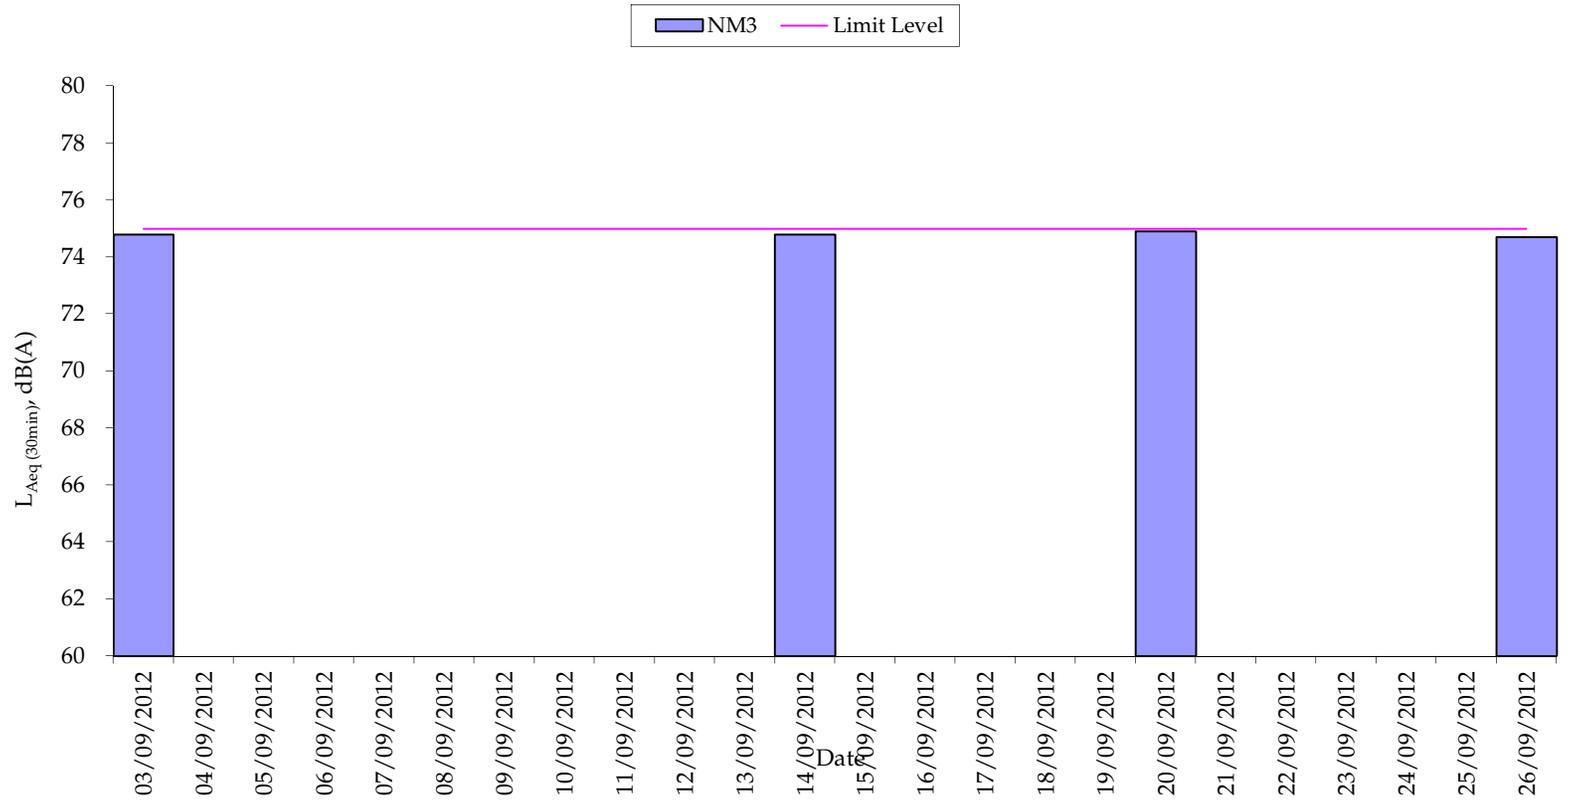

*Annex E7 Cumulative Complaint and Summons/Prosecutions Log*

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
December 2009	0	0
January 2010	0	0
February 2010	0	0
March 2010	0	0
April 2010	0	0
May 2010	0	0
June 2010	0	0
July 2010	0	0
August 2010	0	0
September 2010	0	0
October 2010	0	0
November 2010	0	0
December 2010	0	0
January 2011	0	0
February 2011	0	0
March 2011	0	0
April 2011	0	0
May 2011	0	0

*Annex E7 Cumulative Complaint and Summons/Prosecutions Log*

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
June 2011	0	0
July 2011	0	0
August 2011	0	0
September 2011	0	0
October 2011	0	0
November 2011	0	0
December 2011	0	0
January 2012	0	0
February 2012	0	0
March 2012	0	0
April 2012	0	0
May 2012	0	0
June 2012	0	0
July 2012	0	0
August 2012	0	0
September 2012	0	0
Overall Total	0	0

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	% Comp	2010	2011	2012	2013	2014
<b>HATS Stage 2A - Contract DC/2007/23</b>										
<b>Sai Ying Pun Junction/Production Shaft</b>										
<b>Preliminaries Works</b>										
SYJS10115	SYJS: Construct/Install Blast Protection	2	30APR11	03MAY11	0			ISYJS: Construct/Install Blast Protection		
SYJS10120	SYJS: Site Inspection from Mines	1	04MAY11	04MAY11	0			ISYJS: Site Inspection from Mines		
SYJS10125	SYJS: Issue Blasting Permit	1	05MAY11	05MAY11	0			ISYJS: Issue Blasting Permit		
<b>EBS, Env. &amp; Geotechnical Instrumentations</b>										
<b>Markers/UMP's/Others(Same note as Piez.)</b>										
SYJS0617	SYJS: Install SS Markers (44 Nos.)	50	24OCT09A	06FEB10	68			ISYJS: Install SS Markers (44 Nos.)		
SYJS0619	SYJS: JointSurvey&EstablishBaseline Readings SSM	14	08FEB10	26FEB10	0			ISYJS: JointSurvey&EstablishBaseline Readings SSM		
SYJS0621	SYJS: Install UMP (3 Nos.)	75	01SEP09A	08FEB10	78			ISYJS: Install UMP (3 Nos.)		
SYJS0623	SYJS: JointSurvey&EstablishBaseline Readings UMP	14	09FEB10	27FEB10	0			ISYJS: JointSurvey&EstablishBaseline Readings UMP		
SYJS0625	SYJS: Consent Location and Permits	30	18FEB10	24MAR10	0			ISYJS: Consent Location and Permits		
SYJS0627	SYJS: Install UMP (3 Nos.) Additional	50	25MAR10	24MAY10	0			ISYJS: Install UMP (3 Nos.) Additional		
SYJS0629	SYJS: EstablishBaseline Readings for UMP	14	25MAY10	09JUN10	0			ISYJS: EstablishBaseline Readings for UMP		
<b>Piezometers(NearbyPTWorPScovered inthisInstalln)</b>										
SYJS0407	SYJS: Installation Works of BH851 Piezometer	21	14JAN10A	08FEB10	20			ISYJS: Installation Works of BH851 Piezometer		
SYJS0409	SYJS: BH851 Piezometer Baseline Establishment	26	09FEB10	13MAR10	0			ISYJS: BH851 Piezometer Baseline Establishment		
SYJS0503	SYJS: Installation Works of BH850 Piezometer	21	07DEC09A	29JAN10	57			ISYJS: Installation Works of BH850 Piezometer		
SYJS0507	SYJS: BH850 Piezometer Baseline Establishment	26	30JAN10	04MAR10	0			ISYJS: BH850 Piezometer Baseline Establishment		
SYJS0601A	SYJS: ResolveRestrictions/Rd.AdviceAppr./PrepWrk	33	07NOV09A	27JAN10	79			ISYJS: ResolveRestrictions/Rd.AdviceAppr./PrepWrk		
SYJS0603	SYJS: Installation Works of BH849 Piezometer	21	30JAN10	26FEB10	0			ISYJS: Installation Works of BH849 Piezometer		
SYJS0607	SYJS: BH849 Piezometer Baseline Establishment	26	27FEB10	29MAR10	0			ISYJS: BH849 Piezometer Baseline Establishment		
<b>Electrical &amp; Mechanical Installations</b>										
SYJS0705	SYJS: Installation Works for LV Application	60	11MAR10*	21MAY10	0			ISYJS: Installation Works for LV Application		
SYJS0710	SYJS: LV Connection & Power On	4	22MAY10	26MAY10	0			ISYJS: LV Connection & Power On		
SYJS0720	SYJS: Installation Works for 11KV Application	60	16AUG10*	27OCT10	0			ISYJS: Installation Works for 11KV Application		
SYJS0725	SYJS: 11 KV Connection & Power On	4	28OCT10	01NOV10	0			ISYJS: 11 KV Connection & Power On		
<b>Marine Dumping Permit</b>										
SYJS0370	SYJS: Request for Disposal Site&Get Permit	24	05JAN10A	05FEB10	38			ISYJS: Request for Disposal Site&Get Permit		
<b>Diaphragm Wall</b>										
SYJS0263	SYJS: Excavate 1st Panel to Formation Level	12	04JAN10A	21JAN10	80			ISYJS: Excavate 1st Panel to Formation Level		
SYJS0265	SYJS: 1st Panel Desanding & Preparation Works	5	22JAN10	27JAN10	0			ISYJS: 1st Panel Desanding & Preparation Works		
SYJS0267	SYJS: 1st Panel Rebar Cage Installation	4	28JAN10	01FEB10	0			ISYJS: 1st Panel Rebar Cage Installation		
SYJS0269	SYJS: 1st Panel Concreting Works	1	02FEB10	02FEB10	0			ISYJS: 1st Panel Concreting Works		
SYJS0271	SYJS: Excavate 2nd Panel to Formation Level	12	06JAN10A	02FEB10	60			ISYJS: Excavate 2nd Panel to Formation Level		
SYJS0273	SYJS: 2nd Panel Desanding & Preparation Works	5	03FEB10	08FEB10	0			ISYJS: 2nd Panel Desanding & Preparation Works		
SYJS0275	SYJS: 2nd Panel Rebar Cage Installation	4	09FEB10	12FEB10	0			ISYJS: 2nd Panel Rebar Cage Installation		
SYJS0277	SYJS: 2nd Panel Concreting Works	1	13FEB10	13FEB10	0			ISYJS: 2nd Panel Concreting Works		
SYJS0279	SYJS: Excavate 3rd Panel to Formation Level	12	18FEB10	03MAR10	0			ISYJS: Excavate 3rd Panel to Formation Level		
SYJS0281	SYJS: 3rd Panel Desanding & Preparation Works	5	04MAR10	09MAR10	0			ISYJS: 3rd Panel Desanding & Preparation Works		
SYJS0283	SYJS: 3rd Panel Rebar Cage Installation	4	10MAR10	13MAR10	0			ISYJS: 3rd Panel Rebar Cage Installation		
SYJS0285	SYJS: 3rd Panel Concreting Works	1	15MAR10	15MAR10	0			ISYJS: 3rd Panel Concreting Works		
SYJS0287	SYJS: Excavate 4th Panel to Formation Level	12	16MAR10	29MAR10	0			ISYJS: Excavate 4th Panel to Formation Level		
SYJS0289	SYJS: 4th Panel Desanding & Preparation Works	4	30MAR10	02APR10	0			ISYJS: 4th Panel Desanding & Preparation Works		
SYJS0291	SYJS: 4th Panel Rebar Cage Installation	3	03APR10	07APR10	0			ISYJS: 4th Panel Rebar Cage Installation		
SYJS0293	SYJS: 4th Panel Concreting Works	1	08APR10	08APR10	0			ISYJS: 4th Panel Concreting Works		
SYJS0296	SYJS: Excavate 5th Panel to Formation Level	10	09APR10	20APR10	0			ISYJS: Excavate 5th Panel to Formation Level		
SYJS0298	SYJS: 5th Panel Desanding & Preparation Works	4	21APR10	24APR10	0			ISYJS: 5th Panel Desanding & Preparation Works		
SYJS0301	SYJS: 5th Panel Rebar Cage Installation	2	26APR10	27APR10	0			ISYJS: 5th Panel Rebar Cage Installation		
SYJS0302	SYJS: 5th Panel Concreting Works	1	28APR10	28APR10	0			ISYJS: 5th Panel Concreting Works		
SYJS0304	SYJS: Excavate 6th Panel to Formation Level	10	29APR10	11MAY10	0			ISYJS: Excavate 6th Panel to Formation Level		
SYJS0306	SYJS: 6th Panel Desanding & Preparation Works	4	12MAY10	15MAY10	0			ISYJS: 6th Panel Desanding & Preparation Works		
SYJS0308	SYJS: 6th Panel Rebar Cage Installation	2	17MAY10	18MAY10	0			ISYJS: 6th Panel Rebar Cage Installation		
SYJS0312	SYJS: Excavate 7th Panel to Formation Level	10	20MAY10	31MAY10	0			ISYJS: Excavate 7th Panel to Formation Level		
SYJS0313	SYJS: 6th Panel Concreting Works	1	19MAY10	19MAY10	0			ISYJS: 6th Panel Concreting Works		
SYJS0314	SYJS: 7th Panel Desanding & Preparation Works	4	01JUN10	04JUN10	0			ISYJS: 7th Panel Desanding & Preparation Works		
SYJS0316	SYJS: 7th Panel Rebar Cage Installation	2	05JUN10	07JUN10	0			ISYJS: 7th Panel Rebar Cage Installation		
SYJS0318	SYJS: 7th Panel Concreting Works	1	08JUN10	08JUN10	0			ISYJS: 7th Panel Concreting Works		
SYJS0321	SYJS: Excavate 8th Panel to Formation Level	10	09JUN10	21JUN10	0			ISYJS: Excavate 8th Panel to Formation Level		
SYJS0322	SYJS: 8th Panel Desanding & Preparation Works	4	22JUN10	25JUN10	0			ISYJS: 8th Panel Desanding & Preparation Works		
SYJS0323	SYJS: Grouting Works Phase 1	54	26JUN10	28AUG10	0			ISYJS: Grouting Works Phase 1		
SYJS0324	SYJS: 8th Panel Rebar Cage Installation	2	26JUN10	28JUN10	0			ISYJS: 8th Panel Rebar Cage Installation		
SYJS0326	SYJS: 8th Panel Concreting Works	1	29JUN10	29JUN10	0			ISYJS: 8th Panel Concreting Works		
SYJS0327	SYJS: Excavate 9th Panel to Formation Level	10	30JUN10	12JUL10	0			ISYJS: Excavate 9th Panel to Formation Level		
SYJS0329	SYJS: 9th Panel Desanding & Preparation Works	4	13JUL10	16JUL10	0			ISYJS: 9th Panel Desanding & Preparation Works		
SYJS0331	SYJS: 9th Panel Rebar Cage Installation	2	17JUL10	19JUL10	0			ISYJS: 9th Panel Rebar Cage Installation		
SYJS0333	SYJS: 9th Panel Concreting Works	1	20JUL10	20JUL10	0			ISYJS: 9th Panel Concreting Works		
SYJS0335	SYJS: Excavate 10th Panel to Formation Level	10	21JUL10	31JUL10	0			ISYJS: Excavate 10th Panel to Formation Level		
SYJS0337	SYJS: 10th Panel Desanding & Preparation Works	4	02AUG10	05AUG10	0			ISYJS: 10th Panel Desanding & Preparation Works		
SYJS0339	SYJS: 10th Panel Rebar Cage Installation	2	06AUG10	07AUG10	0			ISYJS: 10th Panel Rebar Cage Installation		
SYJS0341	SYJS: 10th Panel Concreting Works	1	09AUG10	09AUG10	0			ISYJS: 10th Panel Concreting Works		
SYJS0343	SYJS: Excavate 11th Panel to Formation Level	10	10AUG10	20AUG10	0			ISYJS: Excavate 11th Panel to Formation Level		
SYJS0345	SYJS: 11th Panel Desanding & Preparation Works	4	21AUG10	25AUG10	0			ISYJS: 11th Panel Desanding & Preparation Works		
SYJS0347	SYJS: 11th Panel Rebar Cage Installation	2	26AUG10	27AUG10	0			ISYJS: 11th Panel Rebar Cage Installation		
SYJS0349	SYJS: 11th Panel Concreting Works	1	28AUG10	28AUG10	0			ISYJS: 11th Panel Concreting Works		
SYJS0351	SYJS: Excavate 12th Panel to Formation Level	10	30AUG10	09SEP10	0			ISYJS: Excavate 12th Panel to Formation Level		
SYJS0352	SYJS: Grouting Works Phase 2	54	30AUG10	03NOV10	0			ISYJS: Grouting Works Phase 2		
SYJS0353	SYJS: 12th Panel Desanding & Preparation Works	4	10SEP10	14SEP10	0			ISYJS: 12th Panel Desanding & Preparation Works		
SYJS0355	SYJS: 12th Panel Rebar Cage Installation	2	15SEP10	16SEP10	0			ISYJS: 12th Panel Rebar Cage Installation		
SYJS0357	SYJS: 12th Panel Concreting Works	1	17SEP10	17SEP10	0			ISYJS: 12th Panel Concreting Works		
SYJS0359	SYJS: Excavate 13th Panel to Formation Level	10	18SEP10	30SEP10	0			ISYJS: Excavate 13th Panel to Formation Level		
SYJS0361	SYJS: 13th Panel Desanding & Preparation Works	4	02OCT10	06OCT10	0			ISYJS: 13th Panel Desanding & Preparation Works		
SYJS0365	SYJS: 13th Panel Concreting Works	1	09OCT10	09OCT10	0			ISYJS: 13th Panel Concreting Works		
SYJS0367	SYJS: 13th Panel Rebar Cage Installation	2	07OCT10	08OCT10	0			ISYJS: 13th Panel Rebar Cage Installation		
SYJS0368	SYJS: Excavate 14th Panel to Formation Level	10	11OCT10	22OCT10	0			ISYJS: Excavate 14th Panel to Formation Level		
SYJS0369	SYJS: 14th Panel Desanding & Preparation Works	4	23OCT10	27OCT10	0			ISYJS: 14th Panel Desanding & Preparation Works		
SYJS0371	SYJS: 14th Panel Rebar Cage Installation	2	28OCT10	29OCT10	0			ISYJS: 14th Panel Rebar Cage Installation		
SYJS0373	SYJS: 14th Panel Concreting Works	1	30OCT10	30OCT10	0			ISYJS: 14th Panel Concreting Works		




Annex F

## Sai Ying Pun Junction Shaft

**Key**

-  Shaft Excavation Location
-  Site Location

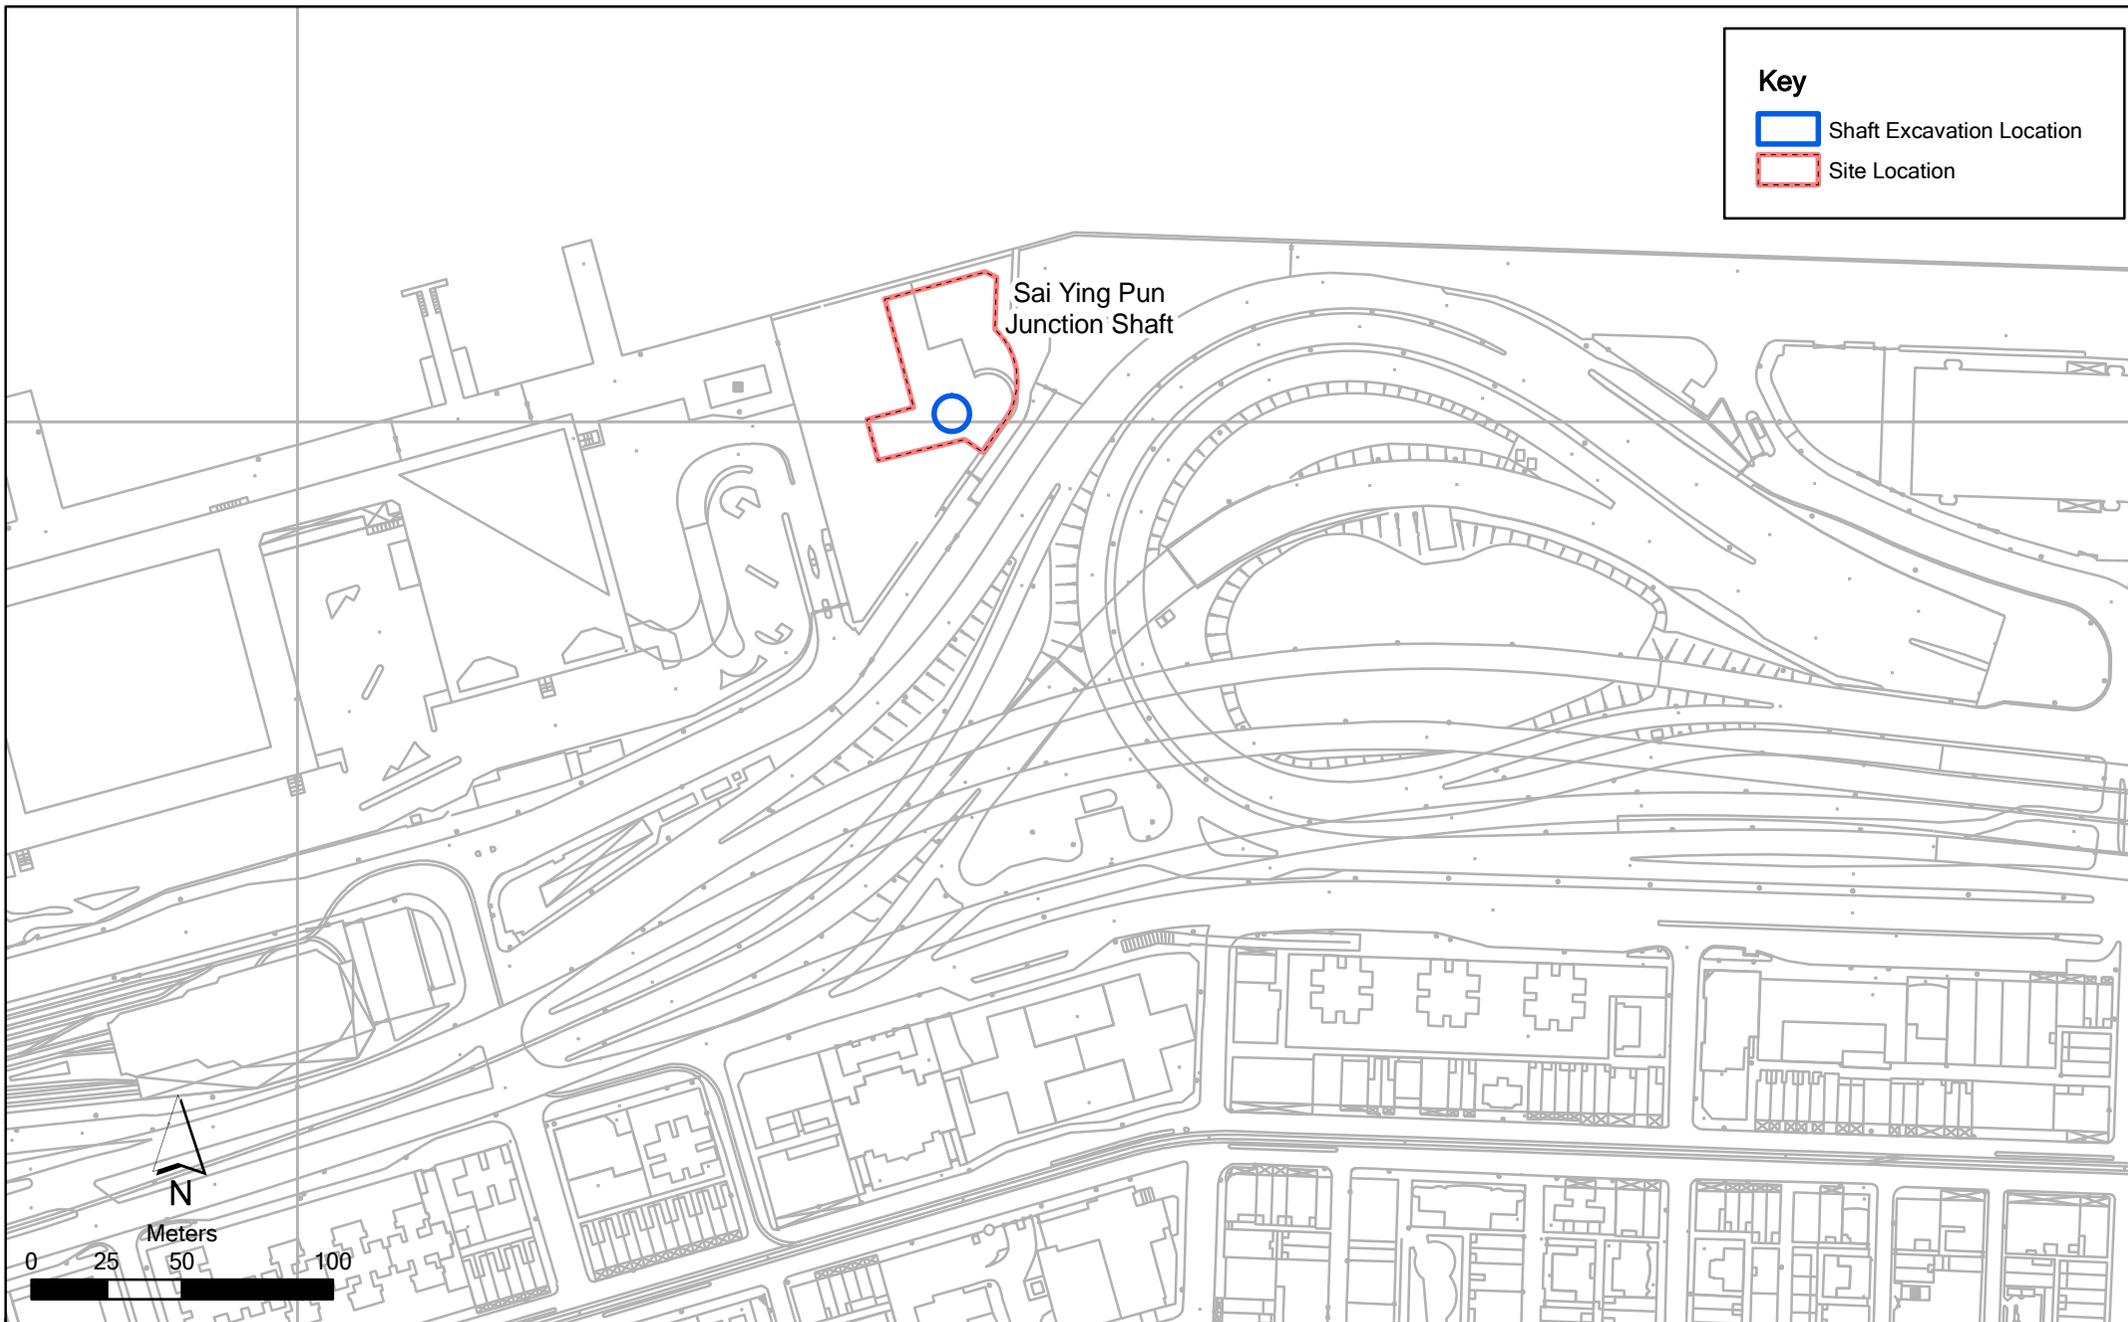

Sai Ying Pun  
Junction Shaft


Annex F1

Contract No. DC/2007/23  
Harbour Area Treatment Scheme Stage 2A  
Construction of Sewage Conveyance System from North Point to Stonecutters Island  
Construction Site Locations at Sai Ying Pun

File: EM&A and proposed station\0104887\_Sai Ying Pun.mxd  
Date: 03/03/2010

**Environmental  
Resources  
Management**



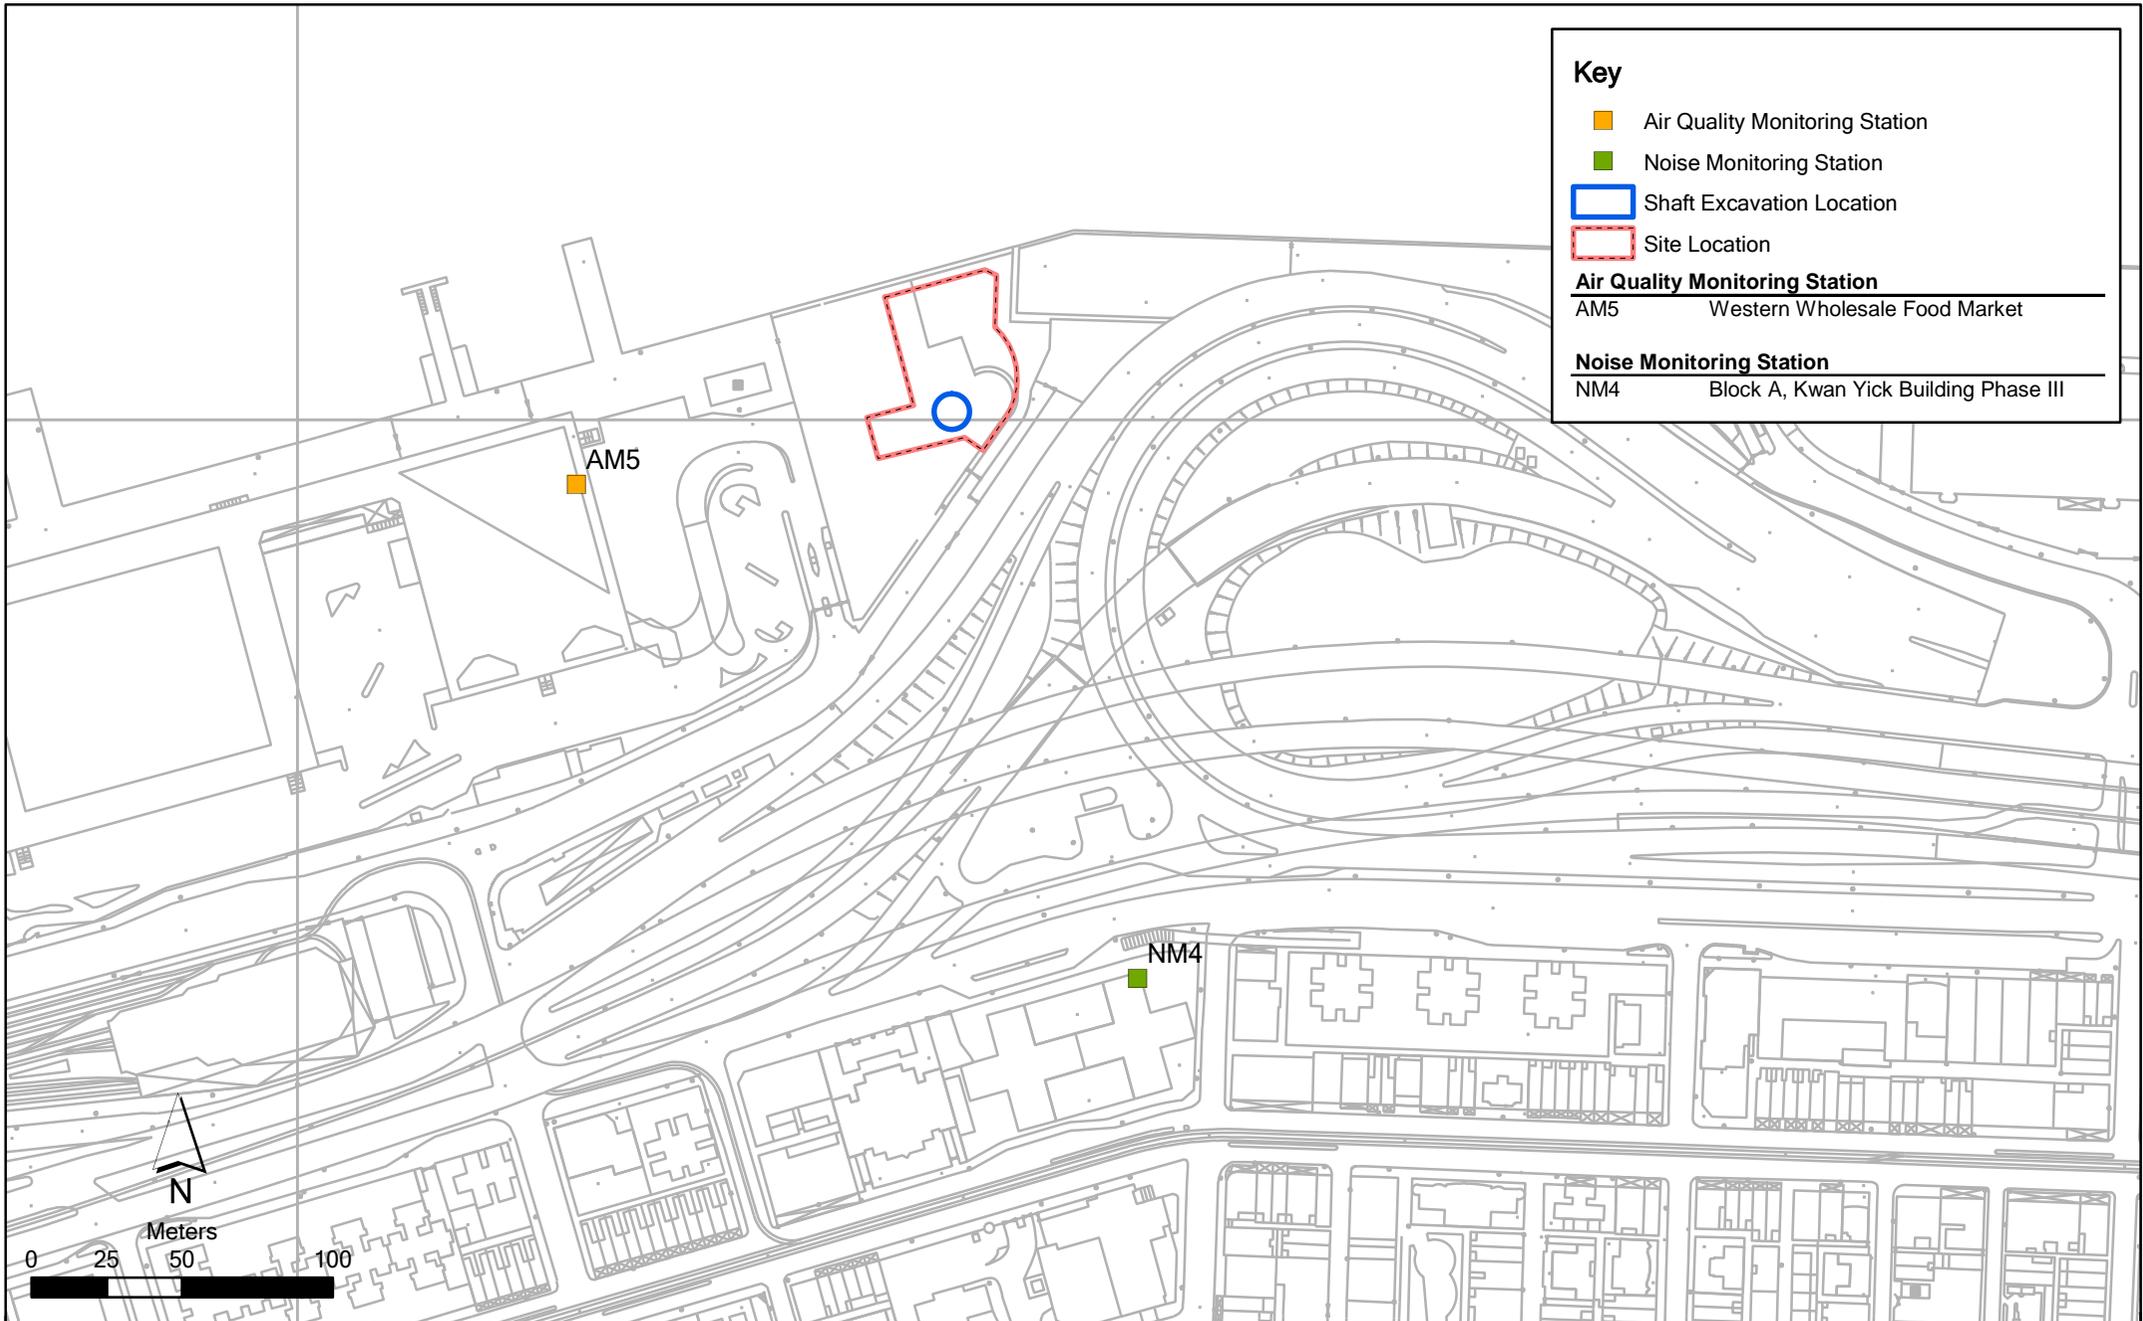

Annex F2

Contract No. DC/2007/23  
 Harbour Area Treatment Scheme Stage 2A  
 Construction of Sewage Conveyance System from North Point to Stonecutters Island  
*Impact Air Quality & Noise Monitoring Stations (Fung Mat Road)*

**Environmental  
 Resources  
 Management**



File: EM&A and proposed station\  
 0104887\_Sai Ting Pun\_NMAM.mxd  
 Date: 03/03/2010



## Annex F3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23

Harbour Area Treatment Scheme Stage 2A

Construction of Sewage Conveyance System from North Point to Stonecutters Island

Impact Construction Air Quality Monitoring Schedule \*

AM5 - Western Wholesale Food Market

Monitoring Month : September 2012

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
		1-hr and 24-hr Monitoring				
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
1-hr and 24-hr Monitoring					1-hr and 24-hr Monitoring	
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
				1-hr and 24-hr Monitoring		
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
		1-hr and 24-hr Monitoring			1-hr and 24-hr Monitoring	
30-Sep						

\* Prepared by Contract No. DC/2007/24 Harbour Area Treatment Scheme Stage 2A (HATS 2A) Construction of Sewage Conveyance System from Aberdeen to Sai Ying Pun

**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
	Public Holiday	Public Holiday	1-hr and 24-hr Monitoring			
7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
	1-hr and 24-hr Monitoring				1-hr and 24-hr Monitoring	
14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
				1-hr and 24-hr Monitoring		
21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct
		Public Holiday	1-hr and 24-hr Monitoring			
28-Oct	29-Oct	30-Oct	31-Oct			
		1-hr and 24-hr Monitoring				

## Annex F3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23

Harbour Area Treatment Scheme Stage 2A

Construction of Sewage Conveyance System from North Point to Stonecutters Island

Impact Construction Noise Quality Monitoring Schedule

NM4 - Block A, Kwan Yick Building Phase III

Monitoring Month : September 2012

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
Noise Monitoring (during daytime of sundays/ public holidays)	Noise Monitoring					
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
		Noise Monitoring (evening time)			Noise Monitoring	
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
Noise Monitoring (during daytime of sundays/ public holidays)				Noise Monitoring		
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
		Noise Monitoring (evening time)	Noise Monitoring			
30-Sep						
Noise Monitoring (during daytime of sundays/ public holidays)						

**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
	Public Holiday	Public Holiday			Noise Monitoring	
7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
		Noise Monitoring (evening time)		Noise Monitoring		
14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
Noise Monitoring (during daytime of sundays/ public holidays)			Noise Monitoring			
21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct
	Noise Monitoring	Noise Monitoring (Evening time) Public Holiday				
28-Oct	29-Oct	30-Oct	31-Oct			
Noise Monitoring (during daytime of sundays/ public holidays)						

**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Construction Phase</i>			
Air Quality	<p>The Air Pollution Control (Construction Dust) Regulation shall be implemented and good site practices shall be incorporated in the contract clauses to minimize construction dust impact. Control measures relevant to this Project are listed below:</p> <ul style="list-style-type: none"> <li>• skip hoist for material transport should be totally enclosed by impervious sheeting;</li> <li>• every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site;</li> <li>• the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;</li> <li>• where a site boundary adjoins a road, streets or other accessible to the public, hoarding of not less than 2.4 m high from ground level should be provided along the entire length except for a site entrance or exit;</li> <li>• every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the 3 sides;</li> <li>• regular watering, with complete coverage, to reduce dust emission from exposed site surfaces and unpaved roads, particularly during dry weather;</li> <li>• site enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines;</li> <li>• open stock piles should be avoided or covered and prevent placing dusty material storage piles near ASRs if possible;</li> <li>• tarpaulin covering of all dusty vehicle loads transported to, from and between site locations; and</li> <li>• instigation of an environmental monitoring auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.</li> </ul>	All work sites / during construction	√

**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Air Quality	<p>The following watering measures for specific site would be required to control the fugitive dust impacts:</p> <ul style="list-style-type: none"> <li>watering twice per day within the worksites at Fung Mat Road Site;</li> <li>the barging points should be continuous watering throughout the whole unloading process.</li> </ul>	All work sites / during construction	√
<i>Operational Phase</i>			
Air Quality	<p>Good housekeeping for SCISTW and PTWs listed below should be followed to ameliorate any odour impact from the plant and these standard practices should be included in the plant operator manual.</p> <ul style="list-style-type: none"> <li>Screens should be cleaned regularly to remove any accumulated organic debris</li> <li>Grit and screening transfer systems should be flushed regularly with water to remove organic debris and grit</li> <li>Grit and screened materials should be transferred to closed containers to minimize odour escape</li> <li>Scum and grease collection wells and troughs should be emptied and flushed regularly to prevent putrefaction of accumulated organics</li> <li>Skim and remove floating solids and grease from primary clarifiers regularly</li> <li>Frequent sludge withdrawal from tanks is necessary to prevent the production of gases</li> <li>Sludge cake should be transferred to closed containers</li> <li>Sludge containers should be flushed with water regularly</li> </ul>	All work sites / during construction	NA. Measures not required until commencement of operational phase
Air Quality	Commissioning tests for all deodorization system should be included in the Design and Construction Contract Document.	All PTW and SCISTW/ during operational phase	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			
Noise	Use of quiet PME, movable barriers and acoustic mats	All work sites / during construction	√

**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Noise	<p>Good Site Practice:</p> <ul style="list-style-type: none"> <li>• only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program;</li> <li>• silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program;</li> <li>• mobile plant, if any, should be sited as far from NSRs as possible;</li> <li>• machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;</li> <li>• plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>• material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities;</li> </ul> <p>Environmental audit shall be carried out to ensure that appropriate noise control measures would be properly implemented.</p>	All work sites / during construction	√
<i>Construction Phase</i>			
Water Quality	<p>Construction Site Runoff and General Construction Activities</p> <p>The mitigation measures as outlined in the ProPECC PN 1/94 Construction Site Drainage should be adopted where applicable.</p>	All work sites / during construction	√

**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Effluent Discharge</p> <p>There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD. Minimum distances of 100 m should be maintained between the discharge points of construction site effluent and the existing saltwater intakes.</p>	All work sites / during construction	√
Water Quality	<p>Accidental Spillage of Chemicals</p> <p>Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.</p>	All work sites / during construction	√
Water Quality	<p>Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.</p>	All work sites / during construction	√



**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes.</p> <p>General requirements are given as follows:</p> <ul style="list-style-type: none"> <li>• Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</li> <li>• Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents.</li> <li>• Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.</li> </ul>	All work sites / during construction	√

**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Construction Works in Close Proximity of Storm Drains or Seafront</p> <p>To minimize the potential water quality impacts from the construction works located at or near any watercourse, the practices outlined below should be adopted where applicable.</p> <ul style="list-style-type: none"> <li>• The use of less or smaller construction plants may be specified to reduce the disturbance to the storm water courses or marine environment.</li> <li>• Temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works.</li> <li>• Stockpiling of construction materials and dusty materials should be covered and located away from any water courses.</li> <li>• Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers.</li> <li>• Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the waterfront, where practicable.</li> <li>• Proper shoring may need to be erected in order to prevent soil/mud from slipping into the storm culvert or sea</li> </ul>	All work sites / during construction	√

**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Operational Phase</i>			
Water Quality	Dual power supply, standby facilities for the main treatment units and standby equipment parts / accessories should be provided as far as possible at the SCISTW to minimize the chance of emergency discharge.	SCISTW and all the Stage 2 PTWs / Operation Stage	NA. Measures not required until commencement of operational phase
Water Quality	Standby unit(s) and dual (backup) power supply would be provided at all the Stage 2 PTWs to reduce the risk of equipment breakdown at the PTWs.	Stage 2 PTWs / Operation Stage	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			
Waste	Reusable steel or concrete panel shutters, fencing and hoarding and signboard should be used as a preferred alternative to items made of wood, to minimise wastage of wood. Attention should be paid to WBTC No. 19/2001 - Metallic Site Hoardings and Signboards to reduce the amount of timber used on construction sites. Metallic alternatives to timber are readily available and should be used rather than new timber. Precast concrete units should be adopted wherever feasible to minimize the use of timber formwork.	All work sites / during the construction period	✓
Waste	All waste materials should be segregated into categories covering: <ul style="list-style-type: none"> <li>• excavated materials suitable for reuse on-site;</li> <li>• excavated materials suitable for public filling facilities;</li> <li>• remaining C&amp;D waste for landfill;</li> <li>• chemical waste; and</li> <li>• general refuse for landfill.</li> </ul>	All work sites / during the construction period	✓

**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	<p>Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> <li>Sort C&amp;D waste from demolition of existing facilities to recover recyclable portions such as metals;</li> <li>Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force;</li> <li>Any unused chemicals or those with remaining functional capacity shall be recycled; and</li> <li>Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> </ul>	All work sites / during the construction period	√
Waste	<p>Recommendations for good site practices during construction activities include:-</p> <ul style="list-style-type: none"> <li>Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site</li> <li>Training of site personnel in proper waste management and chemical waste handling procedures</li> <li>Develop and provide toolbox talk for on-site sorting of C&amp;D materials to enhance worker's awareness in handling, sorting, reuse and recycling of C&amp;D materials.</li> <li>Provision of sufficient waste disposal points and regular collection of waste</li> <li>Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors</li> </ul>	All work sites / during the construction period	√
Waste	Bentonite slurries used in diaphragm wall construction should be reconditioned and reused wherever practicable. The disposal of residual used bentonite slurry should follow the good practice guidelines stated in ProPECC PN 1/94 "Construction Site Drainage".	All work sites / during the construction period	√

**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	Adequate number of portable toilets at temporary works areas or the PTWs to ensure that sewage from site staff would be properly collected.	All work sites / during the construction period	√
Waste	General refuse should be stored in enclosed bins, skips or compaction units separating from C&D material and disposed of at designated landfill.	All work sites / during the construction period	√
Waste	The recyclable component of the municipal waste generated by the workforce, such as aluminium cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.	All work sites / during the construction period	√
Waste	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the approved Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	All work sites / during the construction period	√

**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	Prior to excavation of the marine deposit layer, the deposit should be tested in accordance with the ETWB TC(W) No. 34/2002 and the results should be presented in a Preliminary Sediment Quality Report. The marine deposit should be disposed of at the disposal site designated by the Marine Fill Committee (MFC) or Director of Environmental Protection (DEP) depending on the test results.	All work sites / during the construction period	√
<i>Construction Phase</i>			
Landscape & Visual	<ul style="list-style-type: none"> <li>• Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.</li> <li>• Existing trees to be retained on site should be carefully protected during construction.</li> <li>• Trees unavoidably affected by the works should be transplanted where practical.</li> <li>• Compensatory tree planting should be provided to compensate for felled trees.</li> <li>• Control of night-time lighting.</li> <li>• Erection of decorative screen hoarding compatible with the surrounding setting.</li> </ul>	All the works areas, PTWs and SCISTW/ during the construction period	√
<i>Operational Phase</i>			
Landscape & Visual	<ul style="list-style-type: none"> <li>• Aesthetic design of the façade of PTW and associated structures to harmonize with the surrounding settings.</li> <li>• Shrub and Climbing Plants to soften proposed structures / Roof Greening.</li> <li>• Buffer Tree and Shrub Planting to screen proposed associated structures.</li> <li>• Reinstated of disturbed area</li> </ul>	All the works areas, PTWs and SCISTW/ during the construction period	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			

**ANNEX F4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Cultural Heritage	The construction vibration control limit (ppv of 25mm/s) shall be strictly followed.	Identified historical buildings/structures as mentioned in Tables 15.8 and 15.9. During blasting for tunnel, shafts, effluent conveyance system and disinfection facilities in the vicinity of the buildings/ structures	NA. Vibration monitoring has not been launched during the reporting period.
	Monitoring of vibration limits shall be conducted and reported as a requirement of EM&A programme	Identified historical buildings/structures as mentioned in Tables 15.8 and 15.9. During blasting for tunnel, shafts, effluent conveyance system and disinfection facilities in the vicinity of the buildings/ structures	NA. Vibration monitoring has not been launched during the reporting period.

Remark:

- √ Compliance of Mitigation Measures
- <> Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Limited
- NA Not Applicable

## Annex F5 24-hour and 1-hour TSP Monitoring Results

### 1-hour TSP Monitoring Results

#### Station AM5

Date	Start Time	Finish Time	Weather	TSP Concentration ( $\mu\text{g}/\text{m}^3$ )	Action Level ( $\mu\text{g}/\text{m}^3$ )	Limit Level ( $\mu\text{g}/\text{m}^3$ )	Site Conditions / Observations / Remarks	Temperature ( $^{\circ}\text{C}$ )	Wind Speed * (m/s)	Sampler ID	Filter ID
4-Sep-12	13:00	14:00	Sunny	78	331.9	500	Loading and operation of excavator	28	<5	Western Wholesale Food Market	1173
	14:10	15:10	Sunny	83	331.9	500	Loading and operation of excavator	28	<5	Western Wholesale Food Market	1174
	15:30	16:30	Sunny	59	331.9	500	Loading and operation of excavator	28	<5	Western Wholesale Food Market	1175
10-Sep-12	8:00	9:00	Sunny	219	331.9	500	Loading and operation of excavator	29.3	<5	Western Wholesale Food Market	1181
	9:51	10:51	Sunny	69	331.9	500	Loading and operation of excavator	29.3	<5	Western Wholesale Food Market	1182
	11:00	12:00	Sunny	77	331.9	500	Loading and operation of excavator	29.3	<5	Western Wholesale Food Market	1183
14-Sep-12	8:00	9:00	Sunny	149	331.9	500	Loading and operation of excavator	26.9	<5	Western Wholesale Food Market	1187
	13:50	14:50	Sunny	141	331.9	500	Loading and operation of excavator	26.9	<5	Western Wholesale Food Market	1188
	14:57	15:57	Sunny	150	331.9	500	Loading and operation of excavator	26.9	<5	Western Wholesale Food Market	1189
20-Sep-12	8:00	9:00	Sunny	246	331.9	500	Loading and operation of excavator	27	<5	Western Wholesale Food Market	1194
	13:50	14:50	Sunny	179	331.9	500	Loading and operation of excavator	27	<5	Western Wholesale Food Market	1195
	14:57	15:57	Sunny	187	331.9	500	Loading and operation of excavator	27	<5	Western Wholesale Food Market	1196
25-Sep-12	13:00	14:00	Sunny	87	331.9	500	Loading	27	<5	Western Wholesale Food Market	1201
	14:10	15:10	Sunny	112	331.9	500	Loading	27	<5	Western Wholesale Food Market	1202
	15:30	16:30	Sunny	102	331.9	500	Loading	27	<5	Western Wholesale Food Market	1203
28-Sep-12	8:00	9:00	Sunny	167	331.9	500	works in tunnel	28	<5	Western Wholesale Food Market	1208
	10:40	11:40	Sunny	166	331.9	500	works in tunnel	28	<5	Western Wholesale Food Market	1209
	11:55	12:55	Sunny	233	331.9	500	works in tunnel	28	<5	Western Wholesale Food Market	1210
				<b>Min.</b>	<b>59</b>						
				<b>Max.</b>	<b>246</b>						
				<b>Average</b>	<b>139</b>						

\* Wind Speed data is presented in the Meteorological Data table



## Annex F5 24-hour and 1-hour TSP Monitoring Results

### 24-hour TSP Monitoring Results

#### Station AM5

Start		Finish		Weather	Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m <sup>3</sup> /min)			TSP Conc. (µg/m <sup>3</sup> )	Action Level (µg/m <sup>3</sup> )	Limit Level (µg/m <sup>3</sup> )	Observations / Remarks	Sampler ID	Filter ID
Date	Time	Date	Time		Initial	Final	Initial	Final		Initial	Final	Average						
4-Sep-12	16:45	5-Sep-12	16:45	Sunny	2.6836	2.7430	4556.35	4580.35	24.00	1.11	1.11	1.11	37	188.5	260	Loading and operation of excavator	Western Wholesale Food Market	1176
10-Sep-12	13:00	11-Sep-12	13:00	Sunny	2.6906	2.7621	4583.35	4607.35	24.00	1.11	1.11	1.11	45	188.5	260	Loading and operation of excavator	Western Wholesale Food Market	1184
14-Sep-12	15:45	15-Sep-12	15:45	Sunny	2.6868	2.8513	4610.35	4634.35	24.00	1.10	1.10	1.10	104	188.5	260	Loading and operation of excavator	Western Wholesale Food Market	1190
20-Sep-12	12:10	21-Sep-12	12:10	Sunny	2.6926	2.8509	4637.35	4661.35	24.00	1.10	1.10	1.10	100	188.5	260	Loading and operation of excavator	Western Wholesale Food Market	1197
25-Sep-12	16:35	26-Sep-12	16:35	Sunny	2.6740	2.8142	4664.36	4688.36	24.00	1.10	1.10	1.10	89	188.5	260	Works in tunnel	Western Wholesale Food Market	1204
28-Sep-12	13:11	29-Sep-12	13:11	Sunny	2.6714	2.8788	4691.35	4715.35	24.00	0.99	0.99	0.99	145	188.5	260	Rock out	Western Wholesale Food Market	1211
													Min.	37				
													Max.	145				
													Average	87				

Meteorological Data Extracted from the Hong Kong Observatory

Date	Weather	King's Park Station				
		Average Air Temperature (°C)	Average Relative Humidity (%)	Total Rainfall (mm)	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	5	SE
4/9/2012	Sunny	27	86	17.5	7	E
6/9/2012	Sunny	29	81	2.5	8	E
8/9/2012	Sunny	28.4	79.0	12.0	Not available	Not available
12/9/2012	Sunny	29	78	0.0	9.0	SE
14/9/2012	Sunny	26	63	0.0	9.0	NE
20/9/2012	Sunny	27	79	0.5	Maintenance	E
24/9/2012	Cloudy	32	88	105.0	Maintenance	SE
25/9/2012	Sunny	27	82	20.5	Maintenance	Maintenance
26/9/2012	Cloudy	29	79	0.0	Maintenance	Maintenance
28/9/2012	Sunny	31	53	0.0	18.0	NE
29/9/2012	Sunny	30.8	56.0	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	8.3	N

Date	Weather	Tsing Yi Station				
		Average Air Temperature (°C)	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	27	77	0.0	10	E
4/9/2012	Sunny	28	86	17.5	9	E
6/9/2012	Sunny	30	81	2.5	5	SE
8/9/2012	Sunny	26	79	12.0	Not available	Not available
12/9/2012	Sunny	30	78	0.0	15.0	NE
14/9/2012	Sunny	27	63	0.0	9.0	NW
20/9/2012	Sunny	28	79	0.5	2.0	E
24/9/2012	Cloudy	27	88	105.0	6.0	E
25/9/2012	Sunny	27	82	20.5	8	E
26/9/2012	Cloudy	27	79	0.0	3.0	NE
28/9/2012	Sunny	29	53	0.0	9.0	NW
29/9/2012	Sunny	32	56	0.0	8.0	NW
30/9/2012	Sunny	27	61	0.0	8.0	NW


Date	Weather	Kai Tak Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	12	SE
4/9/2012	Sunny	27	86	17.5	15	E
6/9/2012	Sunny	29	81	2.5	9	NE
8/9/2012	Sunny	28	79	12.0	Not available	Not available
12/9/2012	Sunny	29	78	0.0	10.0	SE
14/9/2012	Sunny	26	63	0.0	12.0	NW
20/9/2012	Sunny	27	79	0.5	16.0	E
24/9/2012	Cloudy	32	88	105.0	6.0	SE
25/9/2012	Sunny	27	82	20.5	20.0	E
26/9/2012	Cloudy	29	79	0.0	5.0	E
28/9/2012	Sunny	31	53	0.0	18.0	N
29/9/2012	Sunny	31	56	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	9.7	N

Date	Weather	Green Island Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	15	NE
4/9/2012	Sunny	27	86	17.5	25	NE
6/9/2012	Sunny	29	81	2.5	30	NE
8/9/2012	Sunny	28	79	12.0	20	Not available
12/9/2012	Sunny	29	78	0.0	9	SE
14/9/2012	Sunny	26	63	0.0	30	N
20/9/2012	Sunny	27	79	0.5	27	NE
24/9/2012	Cloudy	32	88	105.0	8	S
25/9/2012	Sunny	27	82	20.5	35	NE
26/9/2012	Cloudy	29	79	0.0	12	SE
28/9/2012	Sunny	31	53	0.0	25	N
29/9/2012	Sunny	31	56	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	19	N

- \* King's Park's data
- Data were not available
- # less than 24 hourly observations per day


**1-hr TSP Levels  
AM5 (AFCD Western Wholesale Food Market)**

— Action Level — Limit Level ◆ AM5

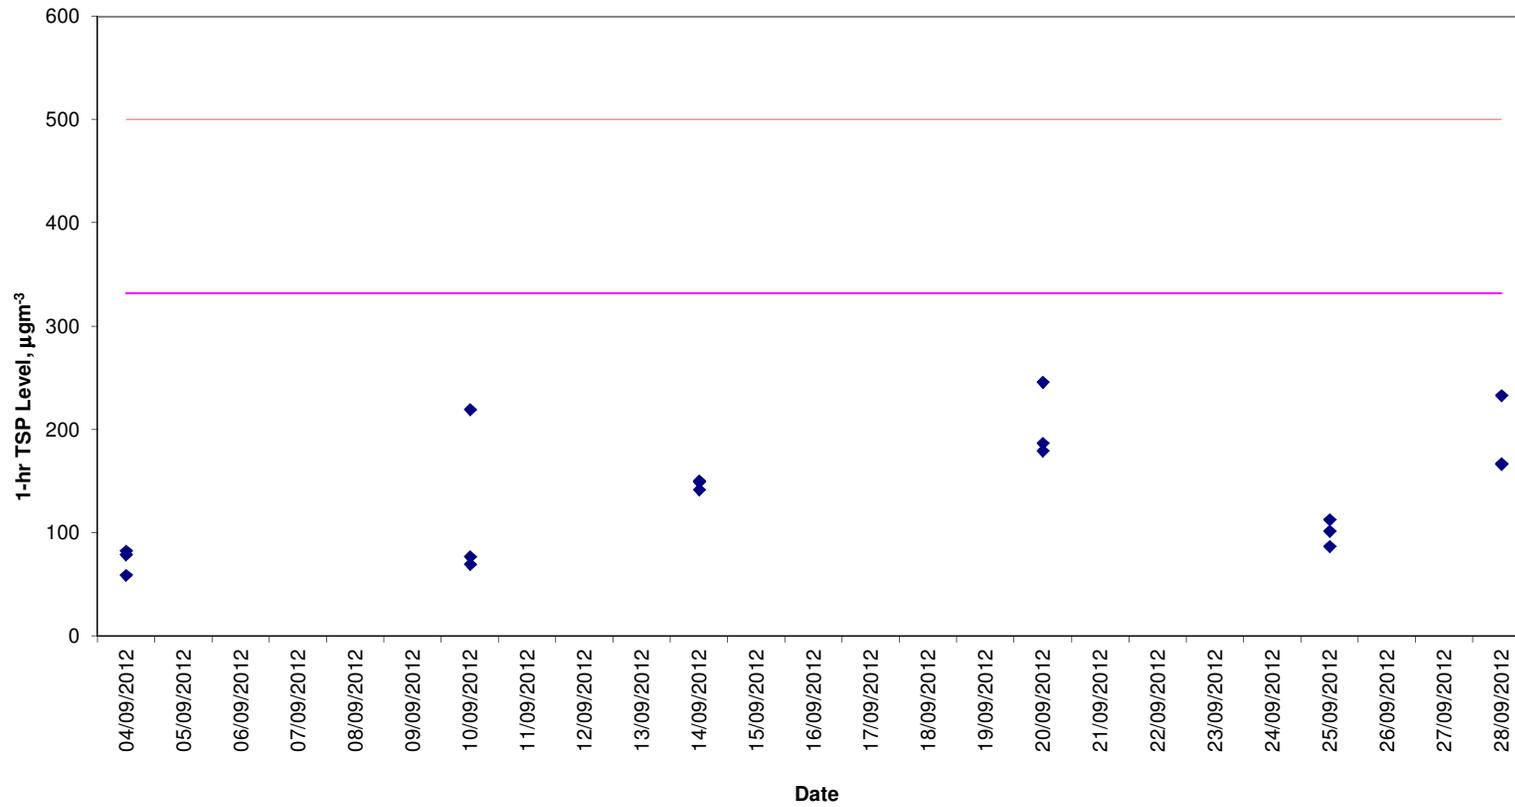

**24-hr TSP Levels  
AM5 (AFCD Western Wholesale Food Market)**


AM5 Action Level Limit Level

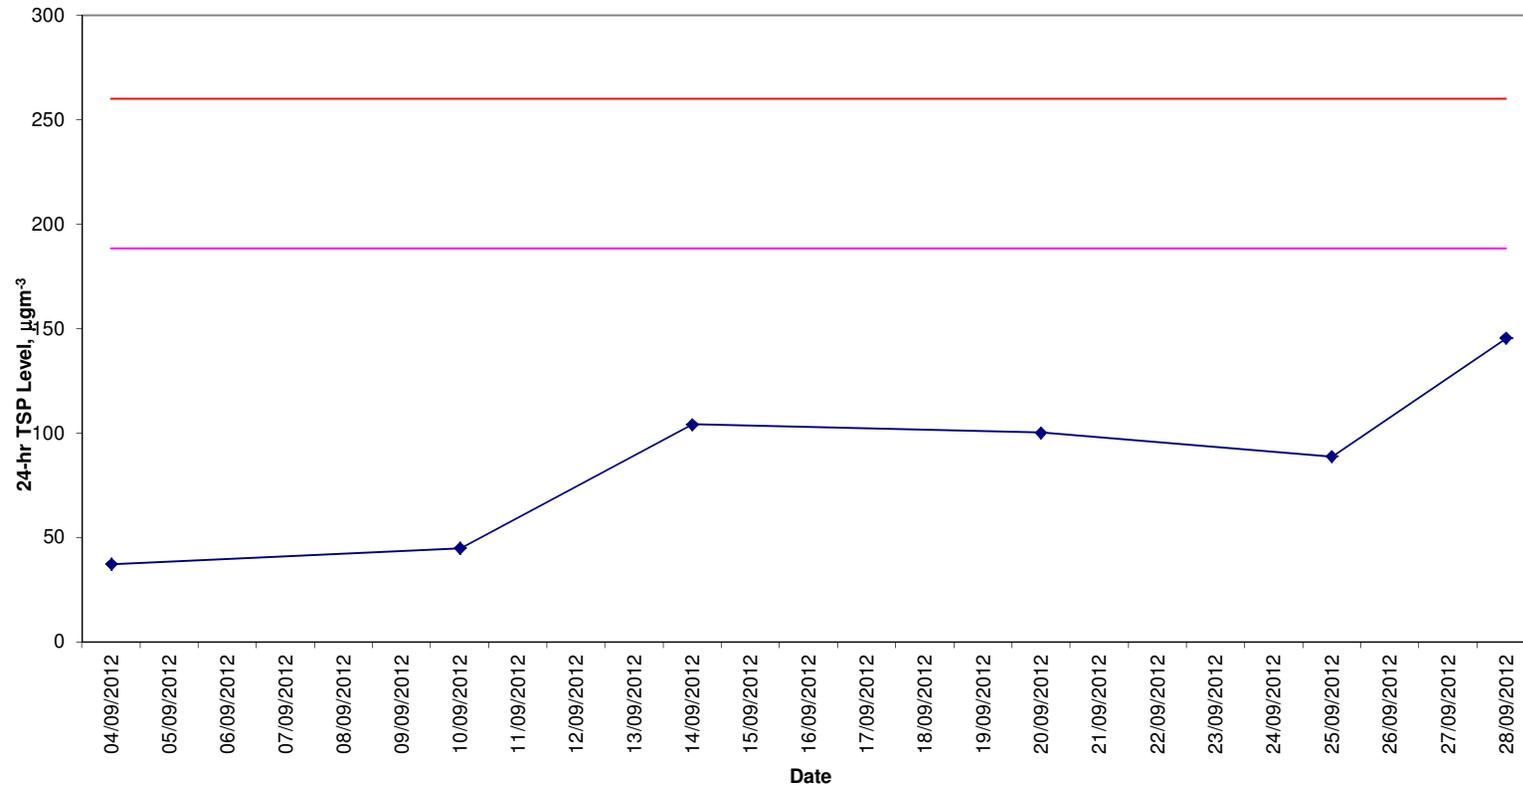






Normal Weekdays Noise Monitoring Results at NM4 ( $L_{eq, 30min}$ )

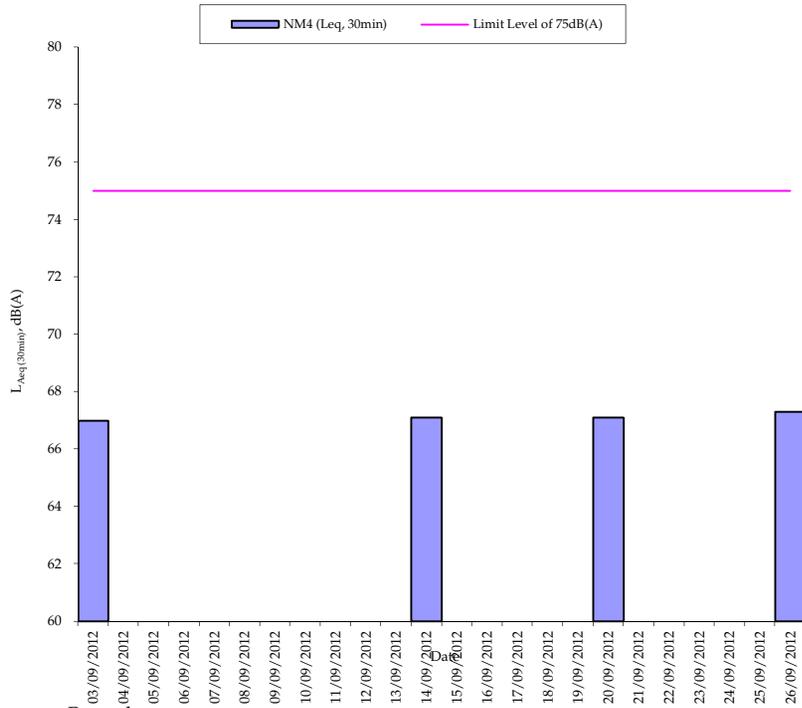

Remark:  
- 75dB(A) was adopted as the Limit Level during normal

Restricted Hours Noise Monitoring Results at NM4 ( $L_{eq, 5min}$ )

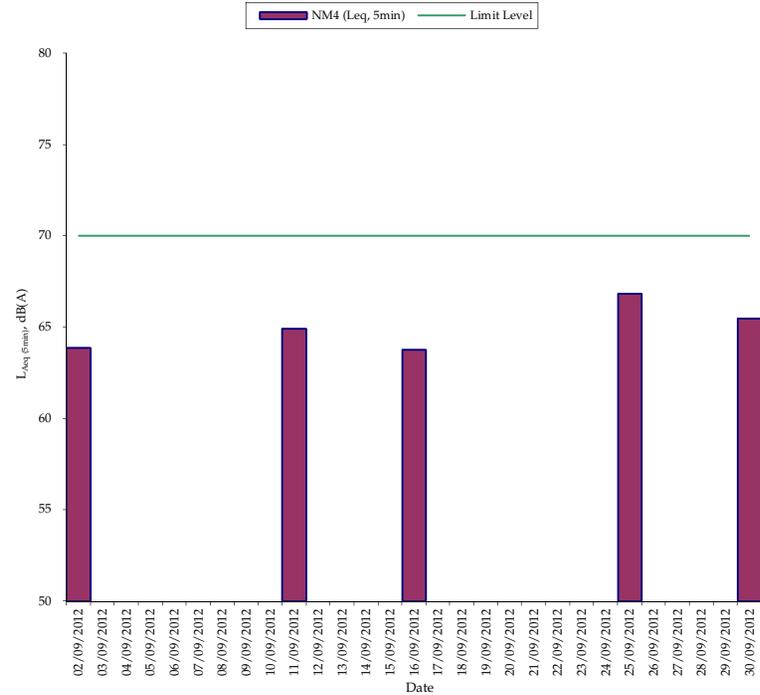

Remark:  
- 70dB(A) was adopted as the Limit Level during restricted hours in the reporting period  
- 55dB(A) was adopted as the Limit Level during night time period

*Annex F7 Cumulative Complaint and Summons/Prosecutions Log*

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
December 2009	0	0
January 2010	0	0
February 2010	1	0
March 2010	0	0
April 2010	1	0
May 2010	2	0
June 2010	0	0
July 2010	1	0
August 2010	0	0
September 2010	0	0
October 2010	0	0
November 2010	0	0
December 2010	0	0
January 2011	0	0
February 2011	0	0
March 2011	0	0
April 2011	0	0
May 2011	0	0



*Annex F7 Cumulative Complaint and Summons/Prosecutions Log*


Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
June 2011	0	0
July 2011	0	0
August 2011	0	0
September 2011	0	0
October 2011	0	0
November 2011	0	0
December 2011	0	0
January 2012	0	0
February 2012	0	0
March 2012	0	0
April 2012	1	0
May 2012	0	0
June 2012	0	0
July 2012	0	0
August 2012	0	0
September 2012	0	0
Overall Total	6	0

Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	% Comp	2010												2011												2012												2013												2014																							
<b>HATS Stage 2A - Contract DC/2007/23</b>																																																																													
<b>Sai Ying Pun Junction/Production Shaft</b>																																																																													
<b>Preliminaries Works</b>																																																																													
SYJS10115	SYJS: Construct/Install Blast Protection	2	30APR11	03MAY11	0																																																																								
SYJS10120	SYJS: Site Inspection from Mines	1	04MAY11	04MAY11	0																																																																								
SYJS10125	SYJS: Issue Blasting Permit	1	05MAY11	05MAY11	0																																																																								
<b>EBS, Env. &amp; Geotechnical Instrumentations</b>																																																																													
<b>Markers/UMP's/Others(Same note as Piez.)</b>																																																																													
SYJS0617	SYJS: Install SS Markers (44 Nos.)	50	24OCT09A	06FEB10	68																																																																								
SYJS0619	SYJS: JointSurvey&EstablishBaseline Readings SSM	14	08FEB10	26FEB10	0																																																																								
SYJS0621	SYJS: Install UMP (3 Nos.)	75	01SEP09A	08FEB10	78																																																																								
SYJS0623	SYJS: JointSurvey&EstablishBaseline Readings UMP	14	09FEB10	27FEB10	0																																																																								
SYJS0625	SYJS: Consent Location and Permits	30	18FEB10	24MAR10	0																																																																								
SYJS0627	SYJS: Install UMP (3 Nos.) Additional	50	25MAR10	24MAY10	0																																																																								
SYJS0629	SYJS: EstablishBaseline Readings for UMP	14	25MAY10	09JUN10	0																																																																								
<b>Piezometers(NearbyPTWorPScovered inthisInstalln)</b>																																																																													
SYJS0407	SYJS: Installation Works of BH851 Piezometer	21	14JAN10A	08FEB10	20																																																																								
SYJS0409	SYJS: BH851 Piezometer Baseline Establishment	26	09FEB10	13MAR10	0																																																																								
SYJS0503	SYJS: Installation Works of BH850 Piezometer	21	07DEC09A	29JAN10	57																																																																								
SYJS0507	SYJS: BH850 Piezometer Baseline Establishment	26	30JAN10	04MAR10	0																																																																								
SYJS0601A	SYJS: ResolveRestrictions/Rd.AdviceAppr./PrepWrk	33	07NOV09A	27JAN10	79																																																																								
SYJS0603	SYJS: Installation Works of BH849 Piezometer	21	30JAN10	26FEB10	0																																																																								
SYJS0607	SYJS: BH849 Piezometer Baseline Establishment	26	27FEB10	29MAR10	0																																																																								
<b>Electrical &amp; Mechanical Installations</b>																																																																													
SYJS0705	SYJS: Installation Works for LV Application	60	11MAR10*	21MAY10	0																																																																								
SYJS0710	SYJS: LV Connection & Power On	4	22MAY10	26MAY10	0																																																																								
SYJS0720	SYJS: Installation Works for 11KV Application	60	16AUG10*	27OCT10	0																																																																								
SYJS0725	SYJS: 11 KV Connection & Power On	4	28OCT10	01NOV10	0																																																																								
<b>Marine Dumping Permit</b>																																																																													
SYJS0370	SYJS: Request for Disposal Site&Get Permit	24	05JAN10A	05FEB10	38																																																																								
<b>Diaphragm Wall</b>																																																																													
SYJS0263	SYJS: Excavate 1st Panel to Formation Level	12	04JAN10A	21JAN10	80																																																																								
SYJS0265	SYJS: 1st Panel Desanding & Preparation Works	5	22JAN10	27JAN10	0																																																																								
SYJS0267	SYJS: 1st Panel Rebar Cage Installation	4	28JAN10	01FEB10	0																																																																								
SYJS0269	SYJS: 1st Panel Concreting Works	1	02FEB10	02FEB10	0																																																																								
SYJS0271	SYJS: Excavate 2nd Panel to Formation Level	12	06JAN10A	02FEB10	60																																																																								
SYJS0273	SYJS: 2nd Panel Desanding & Preparation Works	5	03FEB10	08FEB10	0																																																																								
SYJS0275	SYJS: 2nd Panel Rebar Cage Installation	4	09FEB10	12FEB10	0																																																																								
SYJS0277	SYJS: 2nd Panel Concreting Works	1	13FEB10	13FEB10	0																																																																								
SYJS0279	SYJS: Excavate 3rd Panel to Formation Level	12	18FEB10	03MAR10	0																																																																								
SYJS0281	SYJS: 3rd Panel Desanding & Preparation Works	5	04MAR10	09MAR10	0																																																																								
SYJS0283	SYJS: 3rd Panel Rebar Cage Installation	4	10MAR10	13MAR10	0																																																																								
SYJS0285	SYJS: 3rd Panel Concreting Works	1	15MAR10	15MAR10	0																																																																								
SYJS0287	SYJS: Excavate 4th Panel to Formation Level	12	16MAR10	29MAR10	0																																																																								
SYJS0289	SYJS: 4th Panel Desanding & Preparation Works	4	30MAR10	02APR10	0																																																																								
SYJS0291	SYJS: 4th Panel Rebar Cage Installation	3	03APR10	07APR10	0																																																																								
SYJS0293	SYJS: 4th Panel Concreting Works	1	08APR10	08APR10	0																																																																								
SYJS0296	SYJS: Excavate 5th Panel to Formation Level	10	09APR10	20APR10	0																																																																								
SYJS0298	SYJS: 5th Panel Desanding & Preparation Works	4	21APR10	24APR10	0																																																																								
SYJS0301	SYJS: 5th Panel Rebar Cage Installation	2	26APR10	27APR10	0																																																																								
SYJS0302	SYJS: 5th Panel Concreting Works	1	28APR10	28APR10	0																																																																								
SYJS0304	SYJS: Excavate 6th Panel to Formation Level	10	29APR10	11MAY10	0																																																																								
SYJS0306	SYJS: 6th Panel Desanding & Preparation Works	4	12MAY10	15MAY10	0																																																																								
SYJS0308	SYJS: 6th Panel Rebar Cage Installation	2	17MAY10	18MAY10	0																																																																								
SYJS0312	SYJS: Excavate 7th Panel to Formation Level	10	20MAY10	31MAY10	0																																																																								
SYJS0313	SYJS: 6th Panel Concreting Works	1	19MAY10	19MAY10	0																																																																								
SYJS0314	SYJS: 7th Panel Desanding & Preparation Works	4	01JUN10	04JUN10	0																																																																								
SYJS0316	SYJS: 7th Panel Rebar Cage Installation	2	05JUN10	07JUN10	0																																																																								
SYJS0318	SYJS: 7th Panel Concreting Works	1	08JUN10	08JUN10	0																																																																								
SYJS0321	SYJS: Excavate 8th Panel to Formation Level	10	09JUN10	21JUN10	0																																																																								
SYJS0322	SYJS: 8th Panel Desanding & Preparation Works	4	22JUN10	25JUN10	0																																																																								
SYJS0323	SYJS: Grouting Works Phase 1	54	26JUN10	28AUG10	0																																																																								
SYJS0324	SYJS: 8th Panel Rebar Cage Installation	2	26JUN10	28JUN10	0																																																																								
SYJS0326	SYJS: 8th Panel Concreting Works	1	29JUN10	29JUN10	0																																																																								
SYJS0327	SYJS: Excavate 9th Panel to Formation Level	10	30JUN10	12JUL10	0																																																																								
SYJS0329	SYJS: 9th Panel Desanding & Preparation Works	4	13JUL10	16JUL10	0																																																																								
SYJS0331	SYJS: 9th Panel Rebar Cage Installation	2	17JUL10	19JUL10	0																																																																								
SYJS0333	SYJS: 9th Panel Concreting Works	1	20JUL10	20JUL10	0																																																																								
SYJS0335	SYJS: Excavate 10th Panel to Formation Level	10	21JUL10	31JUL10	0																																																																								
SYJS0337	SYJS: 10th Panel Desanding & Preparation Works	4	02AUG10	05AUG10	0																																																																								
SYJS0339	SYJS: 10th Panel Rebar Cage Installation	2	06AUG10	07AUG10	0																																																																								
SYJS0341	SYJS: 10th Panel Concreting Works	1	09AUG10	09AUG10	0																																																																								
SYJS0343	SYJS: Excavate 11th Panel to Formation Level	10	10AUG10	20AUG10	0																																																																								
SYJS0345	SYJS: 11th Panel Desanding & Preparation Works	4	21AUG10	25AUG10	0																																																																								
SYJS0347	SYJS: 11th Panel Rebar Cage Installation	2	26AUG10	27AUG10	0																																																																								
SYJS0349	SYJS: 11th Panel Concreting Works	1	28AUG10	28AUG10	0																																																																								
SYJS0351	SYJS: Excavate 12th Panel to Formation Level	10	30AUG10	09SEP10	0																																																																								
SYJS0352	SYJS: Grouting Works Phase 2	54	30AUG10	03NOV10	0																																																																								
SYJS0353	SYJS: 12th Panel Desanding & Preparation Works	4	10SEP10	14SEP10	0																																																																								
SYJS0355	SYJS: 12th Panel Rebar Cage Installation	2	15SEP10	16SEP10	0																																																																								
SYJS0357	SYJS: 12th Panel Concreting Works	1	17SEP10	17SEP10	0																																																																								
SYJS0359	SYJS: Excavate 13th Panel to Formation Level	10	18SEP10	30SEP10	0																																																																								
SYJS0361	SYJS: 13th Panel Desanding & Preparation Works	4	02OCT10	06OCT10	0																																																																								
SYJS0365	SYJS: 13th Panel Concreting Works	1	09OCT10	09OCT10	0																																																																								
SYJS0367	SYJS: 13th Panel Rebar Cage Installation	2	07OCT10	08OCT10	0																																																																								
SYJS0368	SYJS: Excavate 14th Panel to Formation Level	10	11OCT10	22OCT10	0																																																																								
SYJS0369	SYJS: 14th Panel Desanding & Preparation Works	4	23OCT10	27OCT10	0																																																																								
SYJS0371	SYJS: 14th Panel Rebar Cage Installation	2	28OCT10	29OCT10	0																																																																								
SYJS0373	SYJS: 14th Panel Concreting Works	1	30OCT10	30OCT10	0																																																																								



Annex G

# Stonecutters Island Production and Riser Shafts

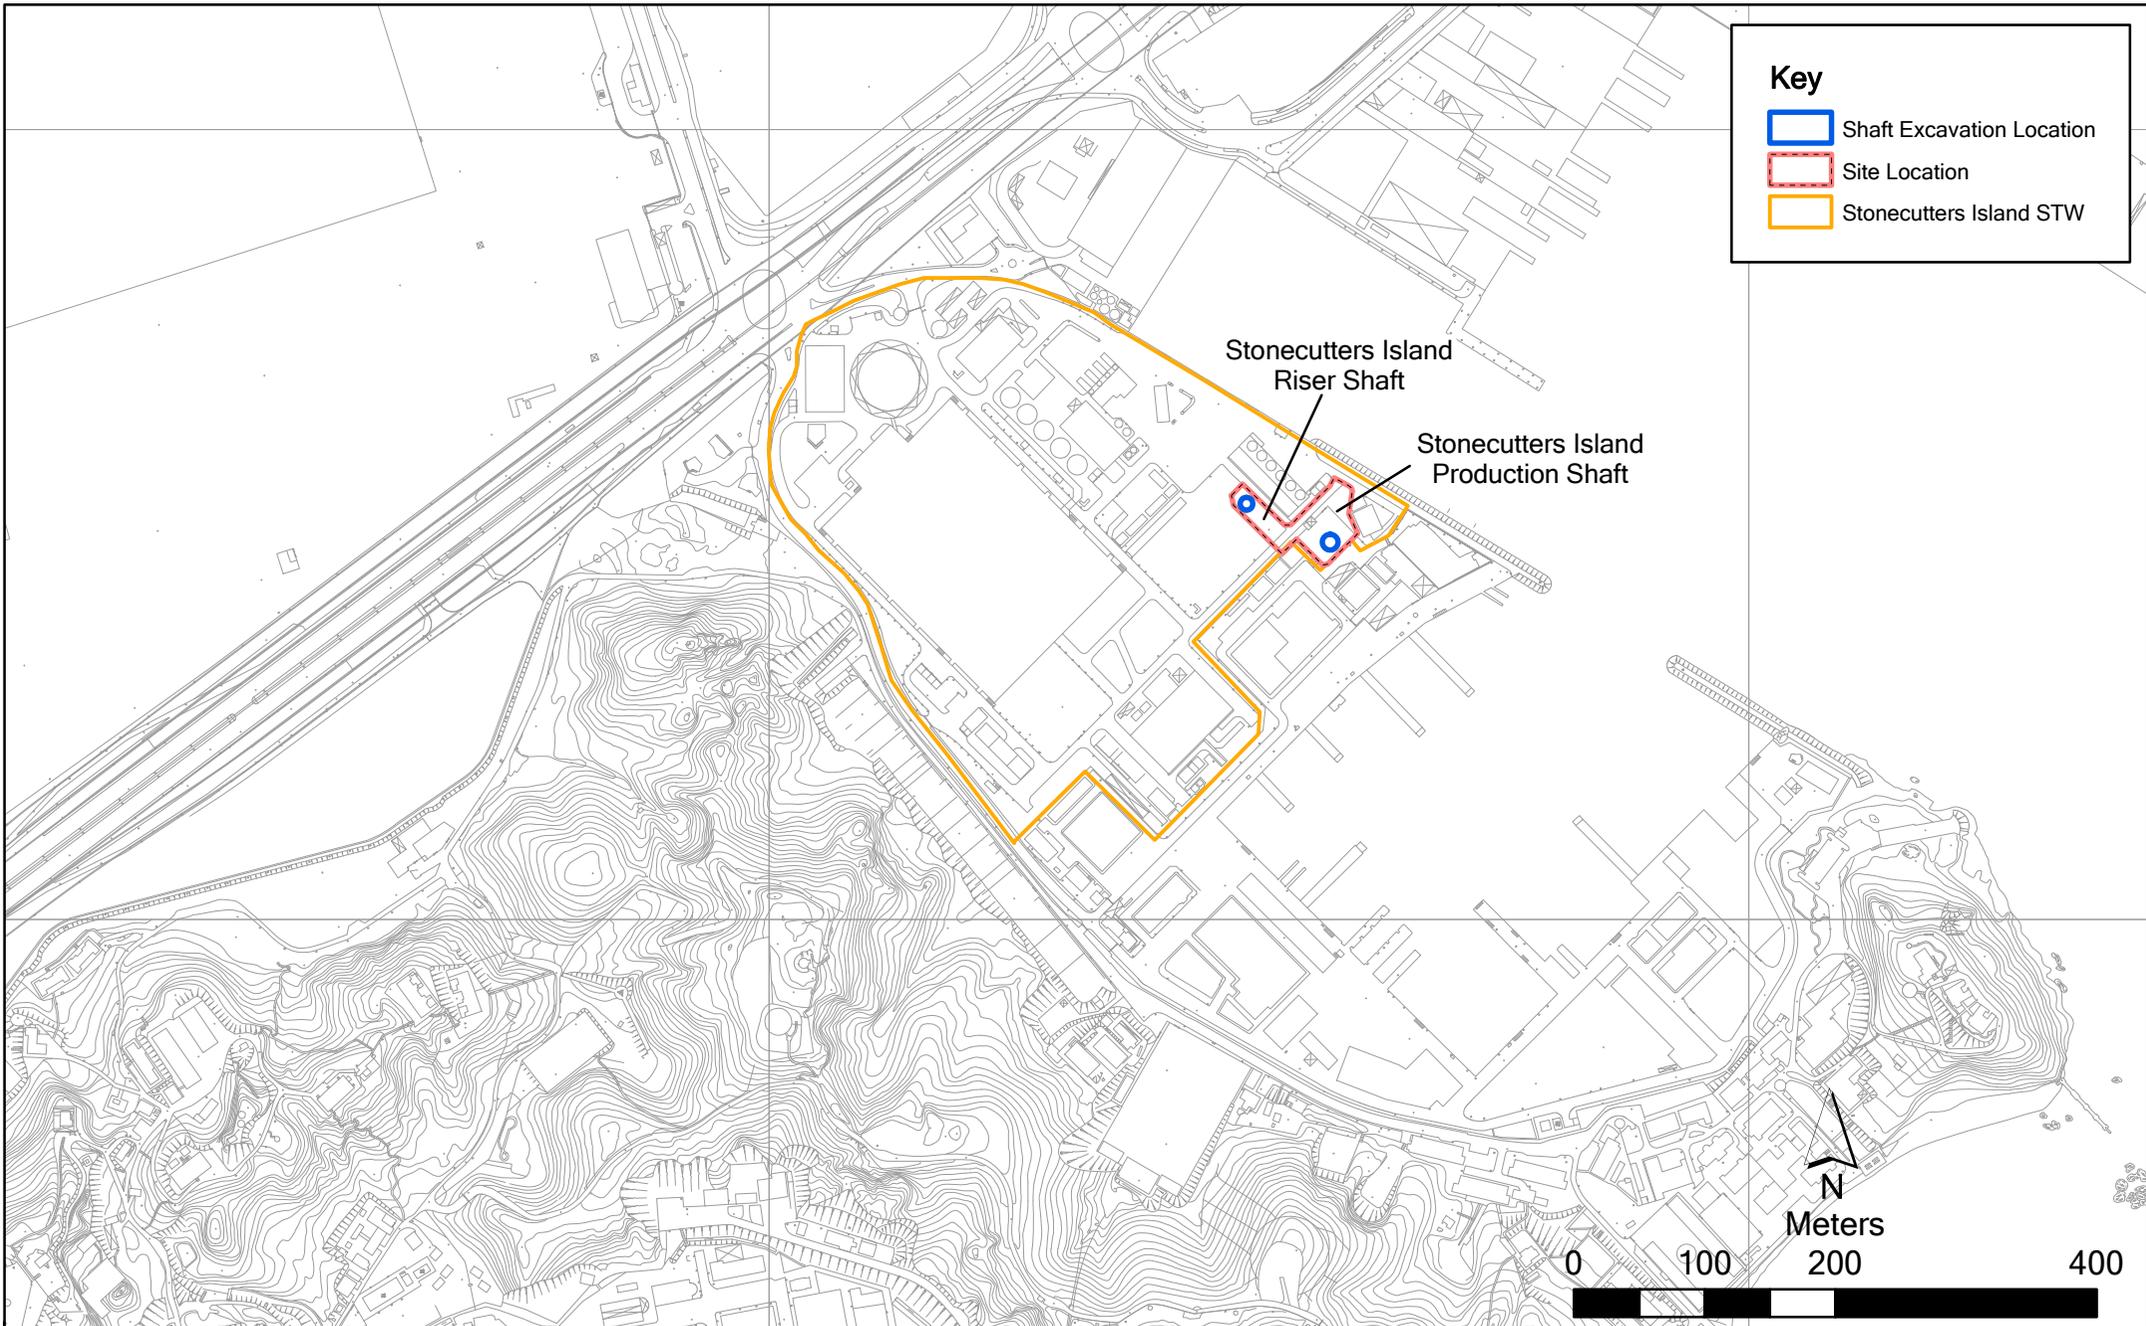


Annex G1

Contract No. DC/2007/23  
 Harbour Area Treatment Scheme Stage 2A  
 Construction of Sewage Conveyance System from North Point to Stonecutters Island  
*Construction Site Locations at Stonecutters Island STW*

File: EM&A and proposed station/  
 0104887\_Stonecutters Island.mxd  
 Date: 03/03/2010

Environmental  
 Resources  
 Management



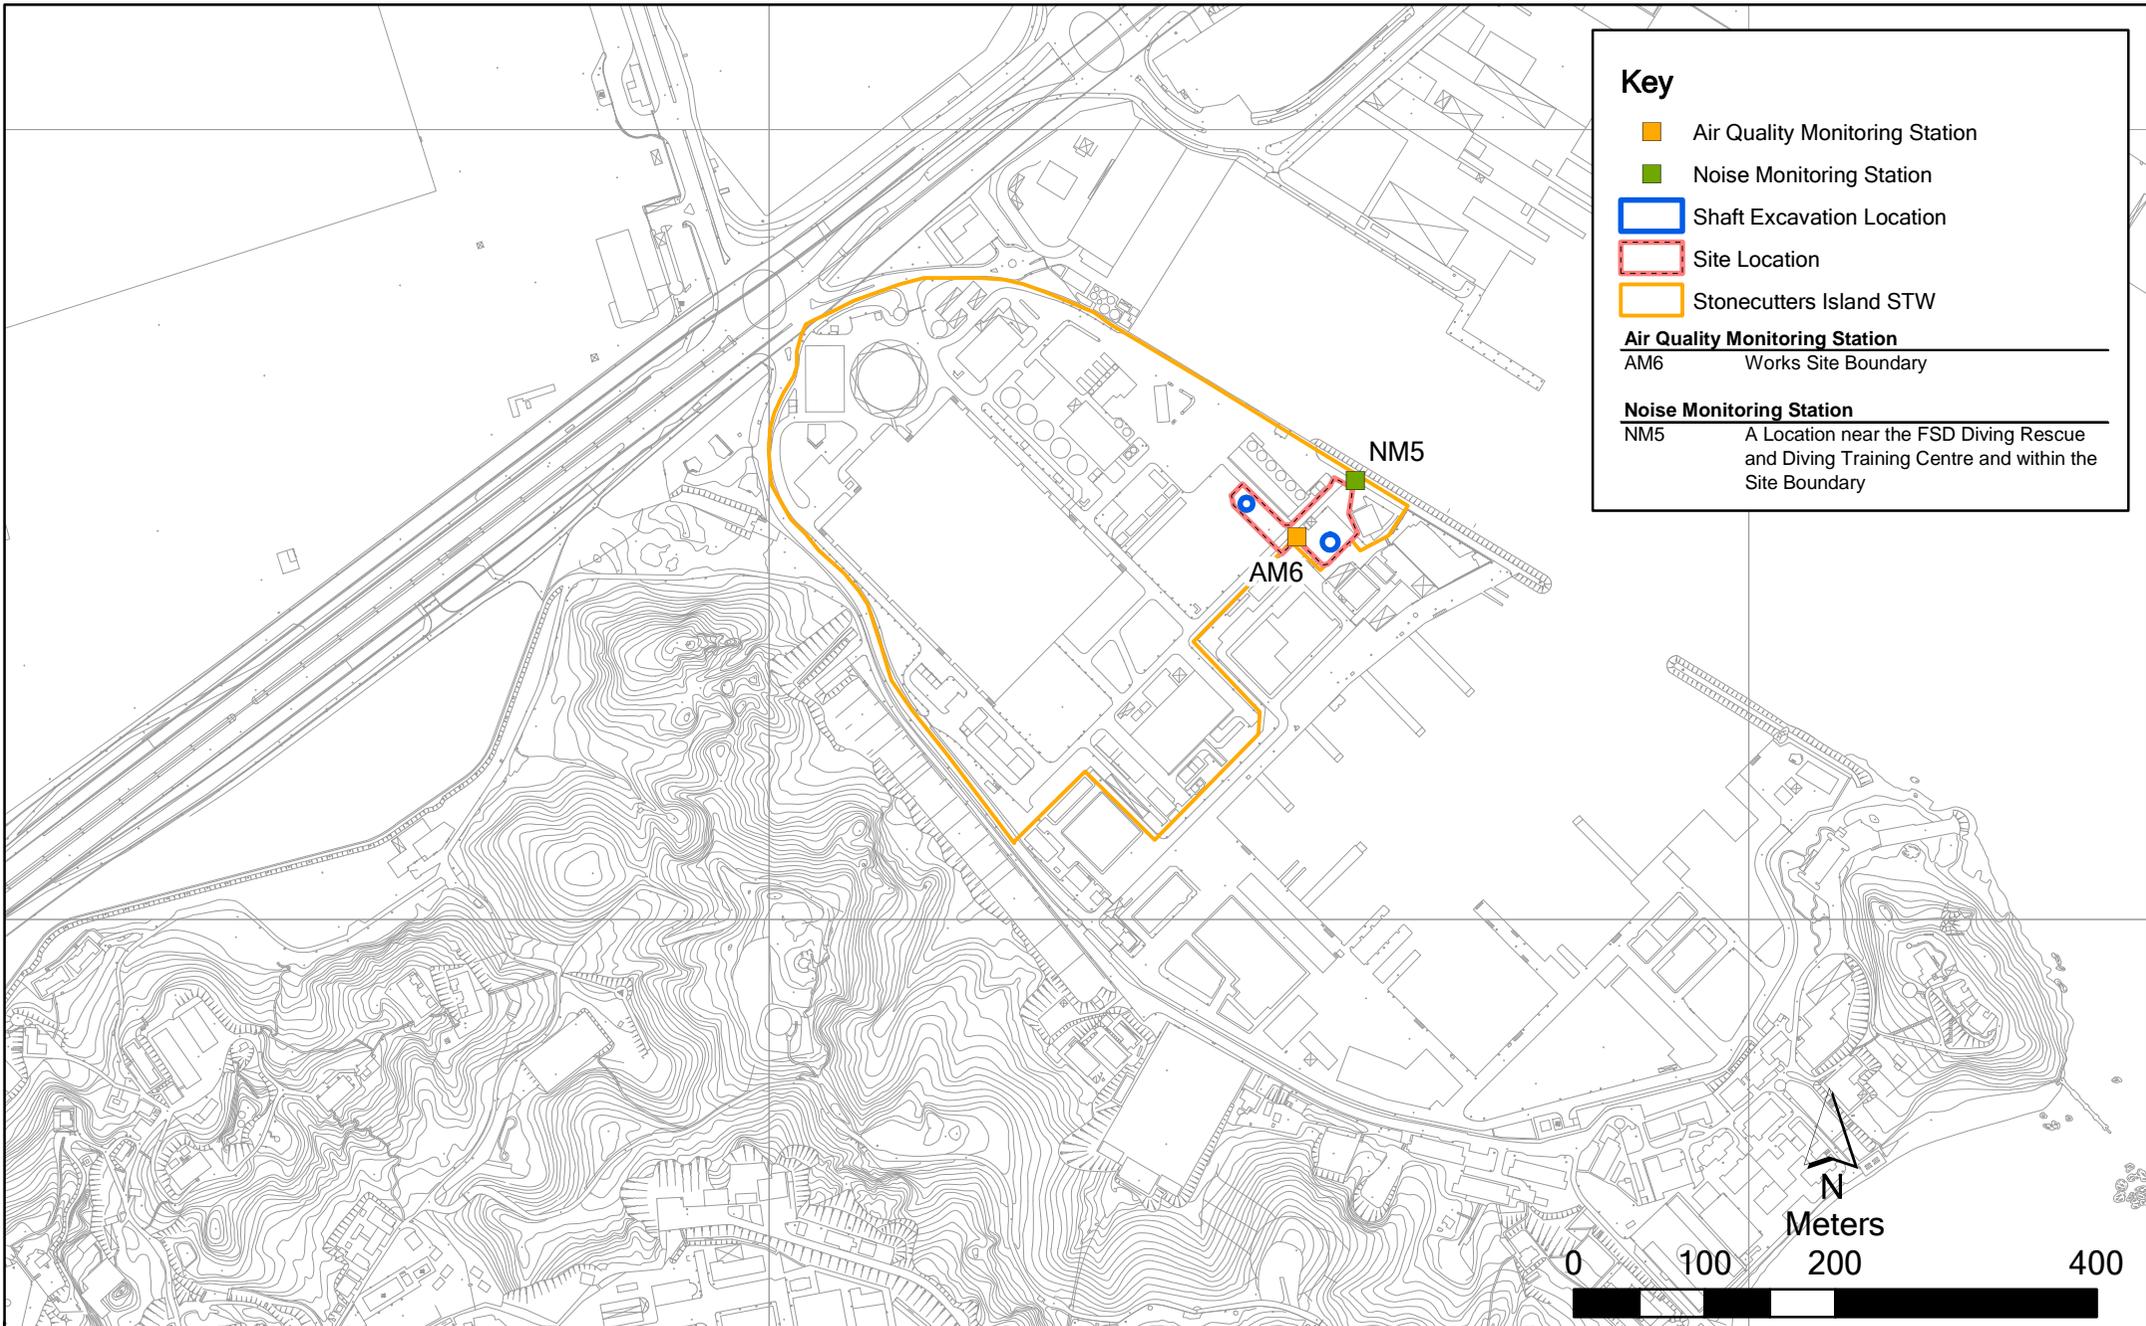

**Key**

- Air Quality Monitoring Station
- Noise Monitoring Station
- Shaft Excavation Location
- Site Location
- Stonecutters Island STW

---

**Air Quality Monitoring Station**

AM6 Works Site Boundary

---

**Noise Monitoring Station**

NM5 A Location near the FSD Diving Rescue and Diving Training Centre and within the Site Boundary

Annex G2

Contract No. DC/2007/23  
 Harbour Area Treatment Scheme Stage 2A  
 Construction of Sewage Conveyance System from North Point to Stonecutters Island  
*Impact Air Quality & Noise Monitoring Station (Stonecutters Island STW)*

File: EM&A and proposed station/  
 0104887\_Stonecutters Island\_NMAM.mxd  
 Date: 03/03/2010

**Environmental  
 Resources  
 Management**



## Annex G3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23

Harbour Area Treatment Scheme Stage 2A

Construction of Sewage Conveyance System from North Point to Stonecutters Island

Impact Construction Air Quality Monitoring Schedule

AM6 - Works Site Boundary

Monitoring Month : September 2012

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
				1-hr and 24-hr Monitoring		
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
			1-hr and 24-hr Monitoring			
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
		1-hr and 24-hr Monitoring				
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
	1-hr and 24-hr Monitoring				1-hr and 24-hr Monitoring	
30-Sep						

**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
	Public Holiday	Public Holiday		1-hr and 24-hr Monitoring		
7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
		1-hr and 24-hr Monitoring				
14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
	1-hr and 24-hr Monitoring				1-hr and 24-hr Monitoring	
21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct
	1-hr and 24-hr Monitoring	Public Holiday		1-hr and 24-hr Monitoring		
28-Oct	29-Oct	30-Oct	31-Oct			
			1-hr and 24-hr Monitoring			



## Annex G3 Monitoring Schedule of the Reporting Month and Next Month

DC/2007/23

Harbour Area Treatment Scheme Stage 2A

Construction of Sewage Conveyance System from North Point to Stonecutters Island

Impact Construction Noise Quality Monitoring Schedule

NM5 - A Location near the FSD Diving Rescue and Diving Training Centre near the Site Boundary

Monitoring Month : September 2012

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Sep
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
		Noise Monitoring (evening time)		Noise Monitoring		
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
Noise Monitoring (during daytime of sundays/ public holidays)			Noise Monitoring			
16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
		Noise Monitoring (Daytime and evening time)				
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep
Noise Monitoring (during daytime of sundays/ public holidays)	Noise Monitoring					
30-Sep						

**Monitoring Month : October 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
	Public Holiday	Public Holiday	Noise Monitoring (Daytime and evening time)	Noise Monitoring		
7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
Noise Monitoring (during daytime of sundays/ public holidays)		Noise Monitoring				
14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
	Noise Monitoring	Noise Monitoring (Daytime and evening time)				
21-Oct	22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct
Noise Monitoring (during daytime of sundays/ public holidays)	Noise Monitoring	Public Holiday		Noise Monitoring		
28-Oct	29-Oct	30-Oct	31-Oct			
		Noise Monitoring (Daytime and evening time)				

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
<i>Construction Phase</i>	<p>The Air Pollution Control (Construction Dust) Regulation shall be implemented and good site practices shall be incorporated in the contract clauses to minimize construction dust impact. Control measures relevant to this Project are listed below:</p> <ul style="list-style-type: none"> <li>• skip hoist for material transport should be totally enclosed by impervious sheeting;</li> <li>• every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site;</li> <li>• the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;</li> <li>• where a site boundary adjoins a road, streets or other accessible to the public, hoarding of not less than 2.4 m high from ground level should be provided along the entire length except for a site entrance or exit;</li> <li>• every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the 3 sides;</li> <li>• regular watering, with complete coverage, to reduce dust emission from exposed site surfaces and unpaved roads, particularly during dry weather;</li> <li>• site enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines;</li> <li>• open stock piles should be avoided or covered and prevent placing dusty material storage piles near ASRs if possible;</li> <li>• tarpaulin covering of all dusty vehicle loads transported to, from and between site locations; and</li> <li>• instigation of an environmental monitoring auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.</li> </ul>	All work sites / during construction	√

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Air Quality	The following watering measures for specific site would be required to control the fugitive dust impacts: <ul style="list-style-type: none"> <li>the barging points should be continuous watering throughout the whole unloading process; and</li> <li>watering 8 times per day within worksites at the SCS works area at SCISTW and the Disinfection Facilities of SCISTW.</li> </ul>	All work sites / during construction	√
<i>Operational Phase</i>			
Air Quality	Good housekeeping for SCISTW and PTWs listed below should be followed to ameliorate any odour impact from the plant and these standard practices should be included in the plant operator manual. <ul style="list-style-type: none"> <li>Screens should be cleaned regularly to remove any accumulated organic debris</li> <li>Grit and screening transfer systems should be flushed regularly with water to remove organic debris and grit</li> <li>Grit and screened materials should be transferred to closed containers to minimize odour escape</li> <li>Scum and grease collection wells and troughs should be emptied and flushed regularly to prevent putrefaction of accumulated organics</li> <li>Skim and remove floating solids and grease from primary clarifiers regularly</li> <li>Frequent sludge withdrawal from tanks is necessary to prevent the production of gases</li> <li>Sludge cake should be transferred to closed containers</li> <li>Sludge containers should be flushed with water regularly</li> </ul>	All work sites / during construction	NA. Measures not required until commencement of operational phase
Air Quality	To avoid excessive extraction of the foul air from the drop shafts of the sedimentation tanks and also from the effluent flume structure of SCISTW to deodorization system, the extraction vent(s) of the deodorization system should be located away from the top openings of the drop shafts.	SCISTW /during operational phase	NA. Measures not required until commencement of operational phase
Air Quality	Commissioning tests for all deodorization system should be included in the Design and Construction Contract Document.	All PTW and SCISTW/ during operational phase	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Noise	Use of quiet PME, movable barriers and acoustic mats	All work sites / during construction	√
Noise	<p>Good Site Practice:</p> <ul style="list-style-type: none"> <li>• only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program;</li> <li>• silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program;</li> <li>• mobile plant, if any, should be sited as far from NSRs as possible;</li> <li>• machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;</li> <li>• plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>• material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities;</li> </ul> <p>Environmental audit shall be carried out to ensure that appropriate noise control measures would be properly implemented.</p>	All work sites / during construction	√
<i>Construction Phase</i>			
Water Quality	<p>Construction Site Runoff and General Construction Activities</p> <p>The mitigation measures as outlined in the ProPECC PN 1/94 Construction Site Drainage should be adopted where applicable.</p>	All work sites / during construction	√

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Effluent Discharge</p> <p>There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD. Minimum distances of 100 m should be maintained between the discharge points of construction site effluent and the existing saltwater intakes.</p>	All work sites / during construction	√
Water Quality	<p>Accidental Spillage of Chemicals</p> <p>Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.</p>	All work sites / during construction	√
Water Quality	<p>Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.</p>	All work sites / during construction	√

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes.</p> <p>General requirements are given as follows:</p> <ul style="list-style-type: none"> <li>• Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</li> <li>• Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents.</li> <li>• Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.</li> </ul>	All work sites / during construction	√

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Construction Works in Close Proximity of Storm Drains or Seafront</p> <p>To minimize the potential water quality impacts from the construction works located at or near any watercourse, the practices outlined below should be adopted where applicable.</p> <ul style="list-style-type: none"> <li>• The use of less or smaller construction plants may be specified to reduce the disturbance to the storm water courses or marine environment.</li> <li>• Temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works.</li> <li>• Stockpiling of construction materials and dusty materials should be covered and located away from any water courses.</li> <li>• Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers.</li> <li>• Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the waterfront, where practicable.</li> <li>• Proper shoring may need to be erected in order to prevent soil/mud from slipping into the storm culvert or sea</li> </ul>	All work sites / during construction	√



**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	<p>Temporary Sewage Bypass</p> <p>It is recommended that the temporary sewage bypass required for (i) the modification to the existing pumping station at SCISTW and (ii) the interconnection between the existing main pumping station and the new pumping station on Stonecutters Island, if needed, should be scheduled at the same time as far as practicable in order to minimise the temporary discharge duration. It is also recommended that all the modification and interconnection to the existing facilities (including the modification to the existing NWKPS) should be programmed to avoid temporary sewage bypass in wet or bathing season (March to October) to minimize the potential impacts. Relevant government departments including EPD and LCSD should be informed of the planned sewage bypass prior to any discharge. During the sewage bypass period, water quality monitoring should be carried out at the water sensitive receivers to quantify the water quality impacts and to determine when the baseline water quality conditions are restored. Also, a framework of the response procedures has been formulated to minimize the impact of temporary discharges. Details are provided in the standalone EM&amp;A Manual.</p>	SCISTW/ construction period	√
<i>Operational Phase</i>			
Water Quality	Dual power supply, standby facilities for the main treatment units and standby equipment parts / accessories should be provided as far as possible at the SCISTW to minimize the chance of emergency discharge.	SCISTW and all the Stage 2 PTWs / Operation Stage	NA. Measures not required until commencement of operational phase
Water Quality	The response procedure and monitoring requirements for emergency discharge as stated in EM&A Manual should be followed.	SCISTW / Operation Stage	NA. Measures not required until commencement of operational phase

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Water Quality	In case of total power outage of the dechlorination plant, the uninterruptible power supply (UPS) system to be provided would switch the power supply of the sodium bisulphite dosing pump to a backup battery almost instantaneously, allowing continuous dosage of sodium bisulphite for at least half an hour so that sufficient time can be provided for shutting down the chlorination plant to avoid the possibility of discharge of chlorinated effluent.	SCISTW / Operation Stage	NA. Measures not required until commencement of operational phase
Water Quality	The model predicted that if Stage 2B is not implemented for HATS in 2021 as scheduled, the nutrient contents (both P and N) in the marine water would ultimately increase to exceed the baseline Stage 1 level when the HATS flow is reaching its design capacity of 2.45M m <sup>3</sup> /day. It is recommended that the future review study for Stage 2B should review the validity of the model predictions provided in this EIA and confirm the need of enhanced nutrient removal for HATS after 2021.	SCISTW / Operation Stage	NA. Measures not required until commencement of operational phase
Water Quality	It should be noted that the mixing zone for TIN predicted for Stage 2B was large with an area of about 30 km <sup>2</sup> and the area of exceedance would encroach on the nearby water sensitive receivers (e.g. Ma Wan Fish Culture Zone). This is due to the elevated oxidized nitrogen assumed for the proposed nitrification process at Stage 2B as well as the increased HATS effluent flow assumed for Stage 2B. It is recommended that these water quality issues should be further investigated / assessed under the future EIA for Stage 2B. Further mitigation measures / alternative treatment designs should also be considered under the future EIA for Stage 2B to mitigate / minimize the potential TIN exceedances.	SCISTW / Operation Stage	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	Reusable steel or concrete panel shutters, fencing and hoarding and signboard should be used as a preferred alternative to items made of wood, to minimise wastage of wood. Attention should be paid to WBTC No. 19/2001 - Metallic Site Hoardings and Signboards to reduce the amount of timber used on construction sites. Metallic alternatives to timber are readily available and should be used rather than new timber. Precast concrete units should be adopted wherever feasible to minimize the use of timber formwork.	All work sites / during the construction period	√
Waste	All waste materials should be segregated into categories covering: <ul style="list-style-type: none"> <li>• excavated materials suitable for reuse on-site;</li> <li>• excavated materials suitable for public filling facilities;</li> <li>• remaining C&amp;D waste for landfill;</li> <li>• chemical waste; and</li> <li>• general refuse for landfill.</li> </ul>	All work sites / during the construction period	√
Waste	Recommendations to achieve waste reduction include: <ul style="list-style-type: none"> <li>• Sort C&amp;D waste from demolition of existing facilities to recover recyclable portions such as metals;</li> <li>• Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>• Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force;</li> <li>• Any unused chemicals or those with remaining functional capacity shall be recycled; and</li> <li>• Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> </ul>	All work sites / during the construction period	√

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	<p>Recommendations for good site practices during construction activities include:-</p> <ul style="list-style-type: none"> <li>• Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site</li> <li>• Training of site personnel in proper waste management and chemical waste handling procedures</li> <li>• Develop and provide toolbox talk for on-site sorting of C&amp;D materials to enhance worker’s awareness in handling, sorting, reuse and recycling of C&amp;D materials.</li> <li>• Provision of sufficient waste disposal points and regular collection of waste</li> <li>• Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors</li> </ul>	All work sites / during the construction period	√
Waste	Bentonite slurries used in diaphragm wall construction should be reconditioned and reused wherever practicable. The disposal of residual used bentonite slurry should follow the good practice guidelines stated in ProPECC PN 1/94 “Construction Site Drainage”.	All work sites / during the construction period	√
Waste	Adequate number of portable toilets at temporary works areas or the PTWs to ensure that sewage from site staff would be properly collected.	All work sites / during the construction period	√
Waste	General refuse should be stored in enclosed bins, skips or compaction units separating from C&D material and disposed of at designated landfill.	All work sites / during the construction period	√
Waste	The recyclable component of the municipal waste generated by the workforce, such as aluminium cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.	All work sites / during the construction period	√

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the approved Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	All work sites / during the construction period	√
Waste	Prior to excavation of the marine deposit layer, the deposit should be tested in accordance with the ETWB TC(W) No. 34/2002 and the results should be presented in a Preliminary Sediment Quality Report. The marine deposit should be disposed of at the disposal site designated by the Marine Fill Committee (MFC) or Director of Environmental Protection (DEP) depending on the test results.	All work sites / during the construction period	√
<i>Operation Phase</i>			
Waste	The sludge tanks should be air-tighten. Rotating brushes or other alternative devises should be installed at the upper frame of the sludge tank washing facilities to provide better cleaning of the surface around the top loading opening of the sludge tanks. Prior to making such provision, the top covers of the sludge transfer tanks should be water cleaned manually after unloading.	SCISTW / Operation Stage	NA. Measures not required until commencement of operational phase

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Waste	Since the air tightness of tankers highly relies on the effectiveness of rubber seals at the loading openings and unloading doors, odour leakage from tankers are commonly resulted from the aging rubber seals. It is recommended to develop a preventive maintenance programme for rubber seals of loading openings and unloading doors of sludge transfer tanks to ensure the tightness of covers and doors. Rubber seals should be regularly replaced within its design life as specified by suppliers.	SCISTW / Operation Stage	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			
Landscape & Visual	<ul style="list-style-type: none"> <li>• Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.</li> <li>• Existing trees to be retained on site should be carefully protected during construction.</li> <li>• Trees unavoidably affected by the works should be transplanted where practical.</li> <li>• Compensatory tree planting should be provided to compensate for felled trees.</li> <li>• Control of night-time lighting.</li> <li>• Erection of decorative screen hoarding compatible with the surrounding setting.</li> </ul>	All the works areas, PTWs and SCISTW / during the construction period	√
<i>Operational Phase</i>			
Landscape & Visual	<ul style="list-style-type: none"> <li>• Aesthetic design of the façade of PTW and associated structures to harmonize with the surrounding settings.</li> <li>• Shrub and Climbing Plants to soften proposed structures / Roof Greening.</li> <li>• Buffer Tree and Shrub Planting to screen proposed associated structures.</li> <li>• Reinstated of disturbed area</li> </ul>	All the works areas, PTWs and SCISTW / during the construction period	NA. Measures not required until commencement of operational phase
<i>Construction Phase</i>			

**ANNEX G4 - SUMMARY OF MITIGATION MEASURES IMPLEMENTATION SCHEDULE**

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Cultural Heritage	The construction vibration control limit (ppv of 25mm/s) shall be strictly followed.	Identified historical buildings/structures as mentioned in Tables 15.10 and 15.11. During blasting for tunnel, shafts, effluent conveyance system and disinfection facilities in the vicinity of the buildings/ structures	NA. Vibration monitoring has not been launched during the reporting period.

Remark:

- √ Compliance of Mitigation Measures
- <> Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Limited
- NA Not Applicable

## Annex G5 24-hour and 1-hour TSP Monitoring Results

### 1-hour TSP Monitoring Results

#### Station AM6

Date	Start Time	Finish Time	Weather	TSP Concentration (µg/m <sup>3</sup> )	Action Level (µg/m <sup>3</sup> )	Limit Level (µg/m <sup>3</sup> )	Site Conditions / Observations / Remarks	Temperature (°C)	Wind Speed * (m/s)	Sampler ID	Filter ID
6-Sep-12	9:00	10:00	Sunny	163	346	500	Construction work in progress	32	<5	1254	5103
	10:02	11:02	Sunny	168	346	500	Construction work in progress	32	<5	1254	5104
	11:04	12:04	Sunny	161	346	500	Construction work in progress	32	<5	1254	5105
12-Sep-12	13:00	14:00	Sunny	172	346	500	Construction work in progress	32	<5	1254	4950
	14:02	15:02	Sunny	165	346	500	Construction work in progress	32	<5	1254	4951
	15:04	16:04	Sunny	159	346	500	Construction work in progress	32	<5	1254	4952
18-Sep-12	9:10	10:10	Sunny	169	346	500	Construction work in progress	30	<5	1254	5249
	10:12	11:12	Sunny	168	346	500	Construction work in progress	30	<5	1254	5250
	11:14	12:14	Sunny	176	346	500	Construction work in progress	30	<5	1254	5251
24-Sep-12	14:05	15:05	Cloudy	180	346	500	Construction work in progress	28	<5	1254	5253
	15:07	16:07	Cloudy	171	346	500	Construction work in progress	28	<5	1254	5254
	16:09	17:09	Cloudy	179	346	500	Construction work in progress	28	<5	1254	5255
28-Sep-12	9:05	10:05	Sunny	179	346	500	Construction work in progress	30	<5	1254	5257
	10:07	11:07	Sunny	160	346	500	Construction work in progress	30	<5	1254	5258
	11:09	12:09	Sunny	168	346	500	Construction work in progress	30	<5	1254	5259
				<b>Min.</b>	<b>159</b>						
				<b>Max.</b>	<b>180</b>						
				<b>Average</b>	<b>169</b>						

\* Wind Speed data is presented in the Meteorological Data table



## Annex G5 24-hour and 1-hour TSP Monitoring Results

### 24-hour TSP Monitoring Results

#### Station AM6

Start		Finish		Weather	Filter Weight (g)		Elapsed Time Reading		Sampling Time (hrs)	Flow Rate (m <sup>3</sup> /min)			TSP Conc. (µg/m <sup>3</sup> )	Action Level (µg/m <sup>3</sup> )	Limit Level (µg/m <sup>3</sup> )	Observations / Remarks	Sampler ID	Filter ID
Date	Time	Date	Time		Initial	Final	Initial	Final		Initial	Final	Average						
6-Sep-12	12:06	7-Sep-12	12:06	Sunny	2.8004	2.9559	10383.03	10407.03	24.00	1.24	1.24	1.24	87	196	260	Construction work in progress	1254	5102
12-Sep-12	16:06	13-Sep-12	16:06	Sunny	2.7991	2.9595	10410.03	10434.03	24.00	1.24	1.24	1.24	90	196	260	Construction work in progress	1254	5101
18-Sep-12	12:16	19-Sep-12	12:16	Sunny	2.7685	2.9144	10437.03	10461.03	24.00	1.24	1.24	1.24	82	196	260	Construction work in progress	1254	5252
24-Sep-12	17:11	25-Sep-12	17:11	Cloudy	2.7702	2.9298	10464.03	10488.03	24.00	1.21	1.21	1.21	92	196	260	Construction work in progress	1254	5256
28-Sep-12	12:11	29-Sep-12	12:11	Sunny	2.7575	2.9056	10491.03	10515.03	24.00	1.21	1.21	1.21	85	196	260	Construction work in progress	1254	5260
													Min.	82				
													Max.	92				
													Average	87				

Meteorological Data Extracted from the Hong Kong Observatory

Date	Weather	King's Park Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	5	SE
4/9/2012	Sunny	27	86	17.5	7	E
6/9/2012	Sunny	29	81	2.5	8	E
8/9/2012	Sunny	28.4	79.0	12.0	Not available	Not available
12/9/2012	Sunny	29	78	0.0	9.0	SE
14/9/2012	Sunny	26	63	0.0	9.0	NE
20/9/2012	Sunny	27	79	0.5	Maintenance	E
24/9/2012	Cloudy	32	88	105.0	Maintenance	SE
25/9/2012	Sunny	27	82	20.5	Maintenance	Maintenance
26/9/2012	Cloudy	29	79	0.0	Maintenance	Maintenance
28/9/2012	Sunny	31	53	0.0	18.0	NE
29/9/2012	Sunny	30.8	56.0	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	8.3	N


Date	Weather	Tsing Yi Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	27	77	0.0	10	E
4/9/2012	Sunny	28	86	17.5	9	E
6/9/2012	Sunny	30	81	2.5	5	SE
8/9/2012	Sunny	26	79	12.0	Not available	Not available
12/9/2012	Sunny	30	78	0.0	15.0	NE
14/9/2012	Sunny	27	63	0.0	9.0	NW
20/9/2012	Sunny	28	79	0.5	2.0	E
24/9/2012	Cloudy	27	88	105.0	6.0	E
25/9/2012	Sunny	27	82	20.5	8	E
26/9/2012	Cloudy	27	79	0.0	3.0	NE
28/9/2012	Sunny	29	53	0.0	9.0	NW
29/9/2012	Sunny	32	56	0.0	8.0	NW
30/9/2012	Sunny	27	61	0.0	8.0	NW

Date	Weather	Kai Tak Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	12	SE
4/9/2012	Sunny	27	86	17.5	15	E
6/9/2012	Sunny	29	81	2.5	9	NE
8/9/2012	Sunny	28	79	12.0	Not available	Not available
12/9/2012	Sunny	29	78	0.0	10.0	SE
14/9/2012	Sunny	26	63	0.0	12.0	NW
20/9/2012	Sunny	27	79	0.5	16.0	E
24/9/2012	Cloudy	32	88	105.0	6.0	SE
25/9/2012	Sunny	27	82	20.5	20.0	E
26/9/2012	Cloudy	29	79	0.0	5.0	E
28/9/2012	Sunny	31	53	0.0	18.0	N
29/9/2012	Sunny	31	56	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	9.7	N


Date	Weather	Green Island Station				
		Average Air Temperature (°C) *	Average Relative Humidity (%) *	Total Rainfall (mm) *	Average Wind Speed (km/h)	Wind Direction
3/9/2012	Sunny	29	77	0.0	15	NE
4/9/2012	Sunny	27	86	17.5	25	NE
6/9/2012	Sunny	29	81	2.5	30	NE
8/9/2012	Sunny	28	79	12.0	20	Not available
12/9/2012	Sunny	29	78	0.0	9	SE
14/9/2012	Sunny	26	63	0.0	30	N
20/9/2012	Sunny	27	79	0.5	27	NE
24/9/2012	Cloudy	32	88	105.0	8	S
25/9/2012	Sunny	27	82	20.5	35	NE
26/9/2012	Cloudy	29	79	0.0	12	SE
28/9/2012	Sunny	31	53	0.0	25	N
29/9/2012	Sunny	31	56	0.0	Not available	Not available
30/9/2012	Sunny	24	61	0.0	19	N

- \* King's Park's data
- Data were not available
- # less than 24 hourly observations per day

**1-hr TSP Levels  
AM6 (Stonecutters Island Sewage Treatment Works)**

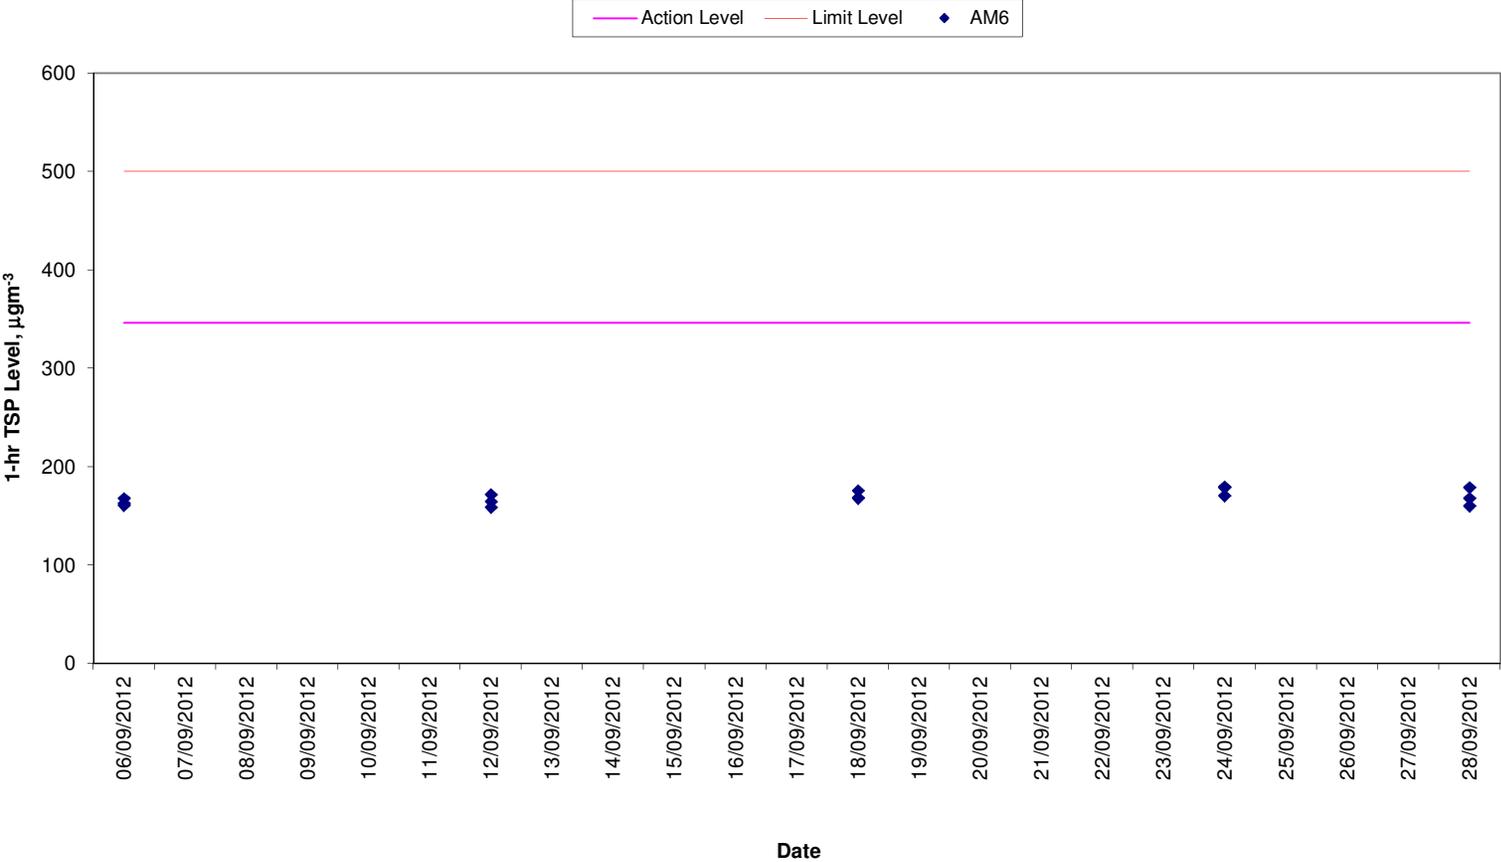

**24-hr TSP Levels  
AM6 (Stonecutters Island Sewage Treatment Works)**

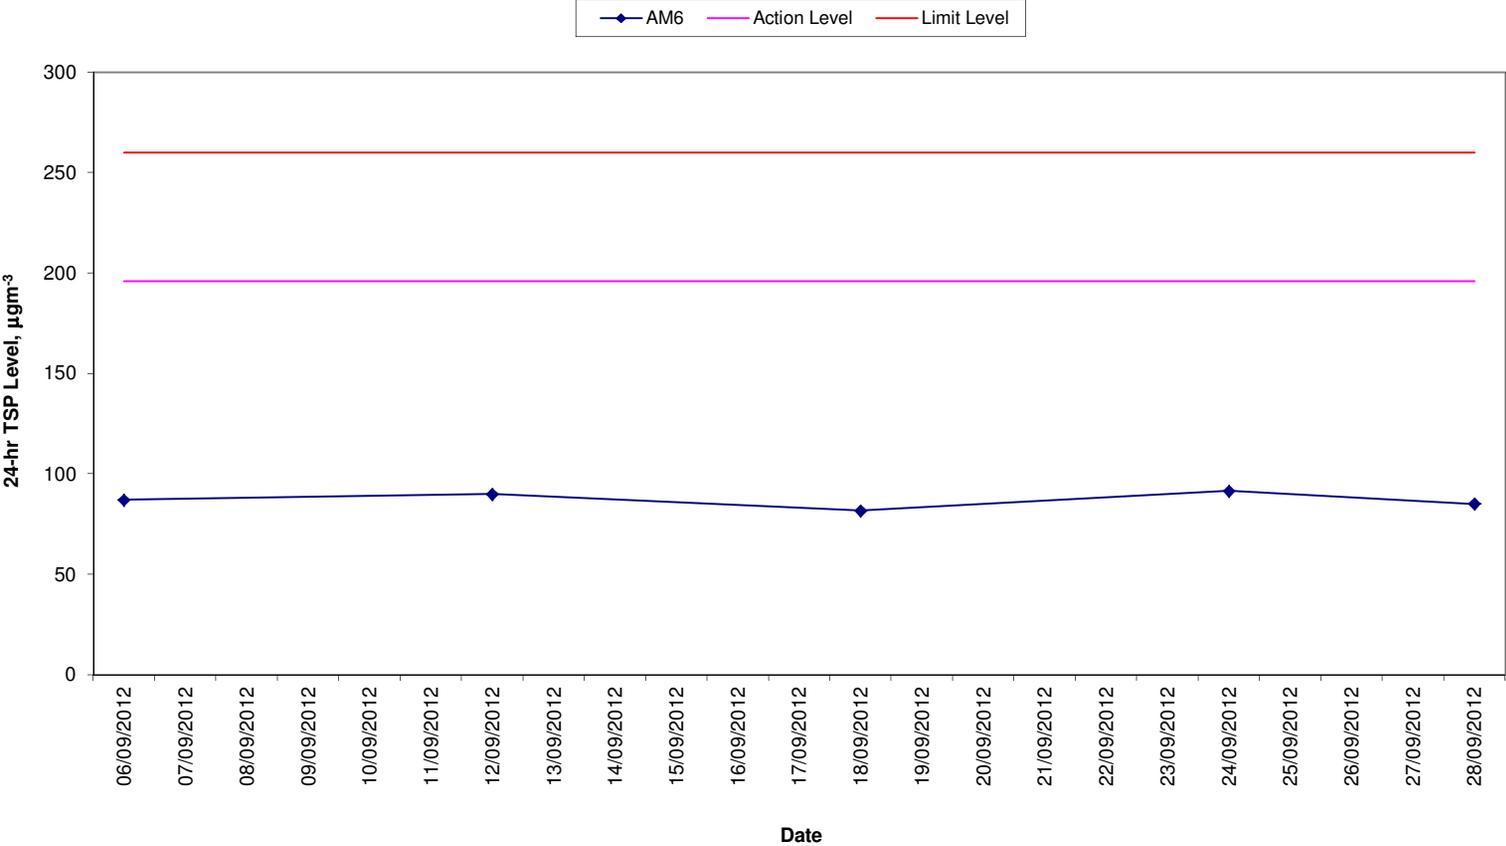




## Annex G6 Noise Monitoring Results

### Restricted Hours Noise Monitoring Results

#### Station NM5


Date	Start Time	End Time	Weather	Noise level (dB(A), 5 min)			Major Construction Noise Source(s) Observed	Other Noise Source(s) Observed	Remarks	Temp. (°C)	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
				Leq	L10	L90							
4-Sep-12	19:30	19:35	Cloudy	61.5	62.8	59.7	Drill rig	Traffic noise	-	32	0.4	RION- NL31 (S/N 00410224)	RION - NC73 (S/N 10997142)
	19:35	19:40	Cloudy	61.1	62.3	59.5			-				
	19:40	19:45	Cloudy	62.0	61.1	60.1			-				
	19:30	19:45	Cloudy	61.5	62.1	59.8			-				
9-Sep-12	13:10	13:15	Sunny	60.4	62.2	58.3	Drill rig	Traffic noise and aircraft noise	-	33	0.3	RION- NL31 (S/N 00410224)	RION - NC73 (S/N 10997142)
	13:15	13:20	Sunny	60.1	62.7	57.7			-				
	13:20	13:25	Sunny	60.2	62.5	57.9			-				
	13:10	13:25	Sunny	60.2	62.5	58.0			-				
18-Sep-12	19:10	19:15	Cloudy	62.2	64.7	58.6	Drill rig	Traffic noise	-	30	0.4	RION- NL31 (S/N 00410224)	RION - NC73 (S/N 10997142)
	19:15	19:20	Cloudy	61.2	63.5	58.5			-				
	19:20	19:25	Cloudy	61.7	63.7	58.6			-				
	19:10	19:25	Cloudy	61.7	64.0	58.6			-				
23-Sep-12	16:00	16:05	Sunny	60.9	61.4	58.4	Drill rig, excavator	Traffic noise & aircraft noise	-	30	0.4	RION- NL31 (S/N 00410224)	RION - NC73 (S/N 10997142)
	16:05	16:10	Sunny	62.3	64.0	59.0			-				
	16:10	16:15	Sunny	61.1	62.7	58.8			-				
	16:00	16:15	Sunny	61.5	62.8	58.7			-				
				<b>Min.</b>	<b>60.1</b>								
				<b>Max.</b>	<b>62.3</b>								

Normal Weekdays Noise Monitoring Results at NM5 ( $L_{eq, 30min}$ )

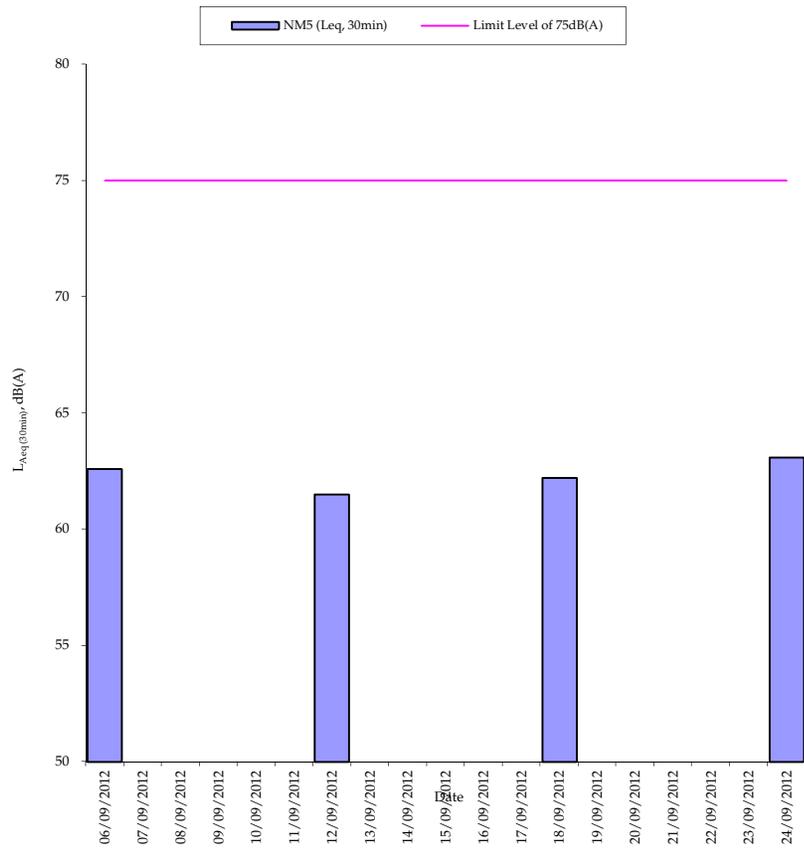

Remark:  
- 75dB(A) was adopted as the Limit Level during normal weekdays in the reporting period

Restricted Hours Noise Monitoring Results at NM5 ( $L_{eq, 5min}$ )

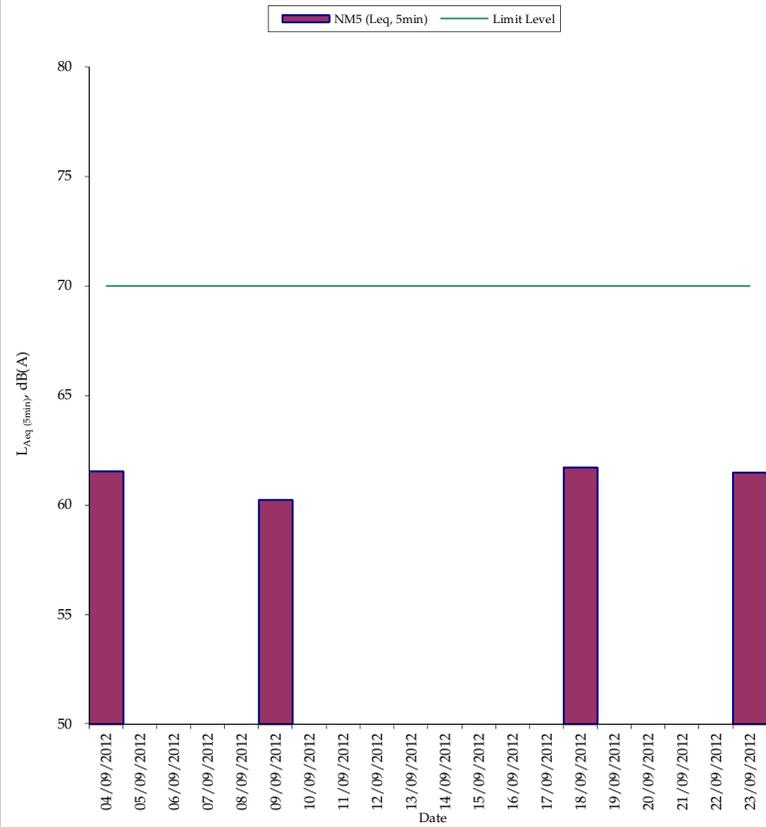

Remark:  
- 70dB(A) was adopted as the Limit Level during restricted hours in the reporting period

*Annex G7 Cumulative Complaint and Summons/Prosecutions Log*

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
December 2009	0	0
January 2010	0	0
February 2010	0	0
March 2010	0	0
April 2010	0	0
May 2010	0	0
June 2010	0	0
July 2010	0	0
August 2010	0	0
September 2010	0	0
October 2010	0	0
November 2010	0	0
December 2010	0	0
January 2011	0	0
February 2011	0	0
March 2011	0	0
April 2011	0	0
May 2011	0	0



*Annex G7 Cumulative Complaint and Summons/Prosecutions Log*

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
June 2011	0	0
July 2011	0	0
August 2011	0	0
September 2011	0	0
October 2011	0	0
November 2011	0	0
December 2011	0	0
January 2012	0	0
February 2012	0	0
March 2012	0	0
April 2012	0	0
May 2012	0	0
June 2012	0	0
July 2012	0	0
August 2012	0	0
September 2012	0	0
Overall Total	0	0





Activity ID	Activity Description	Orig Dur	Early Start	Early Finish	% Comp	2010												2011												2012												2013												2014											
SCRS2060	SCRS: Period of Establishment Works	360	07NOV13	01NOV14	0	SCRS: Period of Establishment Works																																																											
SCRS2070	SCRS: End of Establishment Period	0		01NOV14	0	SCRS: End of Establishment Period																																																											
<b>Connecting Adit</b>																																																																	
SCRS2040	SCRS: Construct RS Connecting Adit	192	14OCT10	03JUN11	0	SCRS: Construct RS Connecting Adit																																																											
SCRS2050	SCRS: Complete Excav & Lining at SCI RS Adit	0		03JUN11	0	SCRS: Complete Excav & Lining at SCI RS Adit																																																											

Start Date 31JUL09  
 Finish Date 15JAN15  
 Data Date 20JAN10  
 Run Date 01FEB10 10:50

 Early Bar  
 Progress Bar  
 Critical Activity

WPU7 Sheet 2 of 2  
**Harbour Area Treatment Scheme Stage 2A**  
 Contract No. DC/2007/23 - Construction of Sewage  
 Conveyance from North Point to Stonecutters Island  
 Programme  
 Annex G8 Construction Programme for the Project



Date	Revision	Checked	Approved

Annex H

# Calibration Reports for Sound Level Meters for All Sites

### *TSP Monitoring Equipment*

<b>Monitoring Station ID</b>	<b>Location</b>	<b>Monitoring Equipment</b>		<b>Last Calibration Date</b>	<b>Next Calibration Date</b>
<i>24-hr and 1-hr TSP</i>		<b>HVS</b>	<b>Calibrator</b>		
AM1	Chan's Creative School (formerly known as Madam Chan Wai Chow Memorial School)	GMW GS-2310 (S/N 1808)	CM-AIR-43 (S/N 0438320)	20 September 2012	20 November 2012
AM2	Rooftop of Hong Kong & Islands Regional Office, WSD	GMW GS-2310 (S/N 0145)	CM-AIR-43 (S/N 0438320)	20 September 2012	20 November 2012
AM3	Rooftop of Wan Chai East PTW	GMW GS-2310 (S/N 0481)	CM-AIR-43 (S/N 0438320)	20 September 2012	20 November 2012
AM4_2	A location next to Sheung Wan Fire Station	GMW GS-2310 (S/N 9315)	CM-AIR-43 (S/N 0438320)	20 September 2012	20 November 2012
AM5	Western Wholesale Food Market	GMW GS-2310 (S/N 2146)	CM-AIR-43 (S/N 0438320)	13 September 2012	13 November 2012
AM6	Works Site Boundary	GMW GS-2310 (S/N 1254)	CM-AIR-43 (S/N 0438320)	20 September 2012	20 November 2012

### Monitoring Equipment

Monitoring Station ID	Monitoring Equipment	Model & Serial No.	Last Calibration Date	Next Calibration Date
NM1 – NM5 <sup>(a)</sup>	Calibrator	Rion NC-73 (S/N 10786708)	17 July 2012	17 July 2013
		Rion NC-73 (S/N 10997142)	9 July 2012	9 July 2013
	Sound Level Meter	Rion NL-52 (S/N 00710259)	20 September 2011	20 September 2012
		Rion NL-31 (S/N 00603867)	18 July 2012	18 July 2013
		Rion NL-31 (S/N 00410224)	15 June 2012	15 June 2013

<sup>(a)</sup> The sound level meter ( Rion NL-52 (S/N 00710259) and Rion NL-31 (S/N 00410224)) and the calibrator (Rion NC-73 (S/N 10786708) or Rion NC-73 (S/N 10997142) ) is used in NM1, NM2, NM3, NM4 and NM5.

### Remarks

Monitoring Station ID	Location
NM1	Rooftop of Chan's Creative School (formerly known as Madam Chan Wai Chow Memorial School)
NM2	Rooftop of Hyde Building
NM3	Rooftop of Goldfield Building
NM4	Rooftop of Block A, Kwan Yick Building Phase III
NM5	A Location near the FSD Diving Rescue and Diving Training Centre near the Site Boundary

High-Volume TSP Sampler  
5-Point Calibration Record

Location : AM1  
Calibrated by : K.T.Ho  
Date : 20/09/2012

Sampler

Model : GMWS-2310 ACCU-VOL  
Serial Number : S/N 1808

Calibration Office and Standard Calibration Relationship

Serial Number : 1378  
Service Date : 22 Feb 2012  
Slope (m) : 1.99405  
Intercept (b) : -0.00397  
Correlation Coefficient(r) : 0.99984

Standard Condition

Pstd (hpa) : 1013  
Tstd (K) : 298.18

Calibration Condition

Pa (hpa) : 1011  
Ta(K) : 300

Resistance Plate	dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1   18 holes	11.7	3.406	1.710	63	62.7
2   13 holes	9.4	3.053	1.533	56	55.8
3   10 holes	6.5	2.538	1.275	46	45.8
4   7 holes	4.9	2.204	1.107	39	38.8
5   5 holes	2.7	1.636	0.822	27	26.9

Sampler Calibration Relationship

Slope(m):40.294 Intercept(b): -5.960 Correlation Coefficient(r): 0.9998

Checked by: Magnum Fan

Date: 24/09/2012



High-Volume TSP Sampler  
5-Point Calibration Record

Location : AM2  
 Calibrated by : K.T.Ho  
 Date : 20/09/2012

Sampler

Model : GMWS-2310 ACCU-VOL  
 Serial Number : S/N 0145

Calibration Office and Standard Calibration Relationship

Serial Number : 1378  
 Service Date : 22 Feb 2012  
 Slope (m) : 1.99405  
 Intercept (b) : -0.00397  
 Correlation Coefficient(r) : 0.99984

Standard Condition

Pstd (hpa) : 1013  
 Tstd (K) : 298.18

Calibration Condition

Pa (hpa) : 1011  
 Ta(K) : 300

Resistance Plate	dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1   18 holes	11.4	3.362	1.688	61	60.7
2   13 holes	9.3	3.036	1.525	55	54.8
3   10 holes	7.3	2.690	1.351	48	47.8
4   7 holes	4.6	2.135	1.073	37	36.8
5   5 holes	2.9	1.696	0.852	29	28.9

Sampler Calibration Relationship

Slope(m):38.463 Intercept(b): -4.116 Correlation Coefficient(r): 0.9998

Checked by: Magnum Fan

Date: 24/09/2012

High-Volume TSP Sampler  
5-Point Calibration Record

Location : AM3  
 Calibrated by : K.T.Ho  
 Date : 20/09/2012

Sampler

Model : GMWS-2310 ACCU-VOL  
 Serial Number : S/N 0481

Calibration Office and Standard Calibration Relationship

Serial Number : 1378  
 Service Date : 22 Feb 2012  
 Slope (m) : 1.99405  
 Intercept (b) : -0.00397  
 Correlation Coefficient(r) : 0.99984

Standard Condition

Pstd (hpa) : 1013  
 Tstd (K) : 298.18

Calibration Condition

Pa (hpa) : 1011  
 Ta(K) : 300

Resistance Plate	dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1   18 holes	11.5	3.377	1.695	62	61.7
2   13 holes	8.8	2.954	1.483	53	52.8
3   10 holes	7.0	2.634	1.323	47	46.8
4   7 holes	4.7	2.159	1.085	36	35.8
5   5 holes	2.8	1.666	0.838	26	25.9

Sampler Calibration Relationship

Slope(m):41.959 Intercept(b): -9.299 Correlation Coefficient(r): 0.9997

Checked by: Magnum Fan

Date: 24/09/2012

High-Volume TSP Sampler  
5-Point Calibration Record

Location : AM4\_2  
 Calibrated by : K.T.Ho  
 Date : 20/09/2012

Sampler

Model : GMWS-2310 ACCU-VOL  
 Serial Number : S/N 9315

Calibration Office and Standard Calibration Relationship

Serial Number : 1378  
 Service Date : 22 Feb 2012  
 Slope (m) : 1.99405  
 Intercept (b) : -0.00397  
 Correlation Coefficient(r) : 0.99984

Standard Condition

Pstd (hpa) : 1013  
 Tstd (K) : 298.18

Calibration Condition

Pa (hpa) : 1011  
 Ta(K) : 300

Resistance Plate	dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1   18 holes	10.4	3.211	1.612	62	61.7
2   13 holes	8.4	2.886	1.449	55	54.8
3   10 holes	6.7	2.577	1.294	48	47.8
4   7 holes	4.6	2.135	1.073	38	37.8
5   5 holes	2.7	1.636	0.822	28	27.9

Sampler Calibration Relationship

Slope(m):40.958 Intercept(b): -6.834 Correlation Coefficient(r): 0.9999

Checked by: Magnum Fan

Date: 24/09/2012

ENVIROTECH SERVICES CO.

**High-Volume TSP Sampler**  
**5-Point Calibration Record**

Location : Sai Ying Pun  
Calibrated by : K.F.Ho  
Date : 13/09/2012

**Sampler**

Model : TE-5170  
Serial Number : S/N 2146

**Calibration Orifice and Standard Calibration Relationship**

Serial Number : 1378  
Service Date : 22 Feb 2012  
Slope (m) : 1.99405  
Intercept (b) : -0.00397  
Correlation Coefficient(r) : 0.99984

**Standard Condition**

Pstd (hpa) : 1013  
Tstd (K) : 298.18

**Calibration Condition**

Pa (hpa) : 1009  
Ta(K) : 302

Resistance Plate	dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1   18 holes	11.1	3.303	1.658	60	59.5
2   13 holes	9.7	3.088	1.550	55	54.5
3   10 holes	7.9	2.7871	1.399	50	49.6
4   7 holes	4.8	2.172	1.091	38	37.7
5   5 holes	2.8	1.659	0.834	28	27.8

**Sampler Calibration Relationship**

Slope(m): 38.059 Intercept(b): -3.929 Correlation Coefficient(r): 0.9996

Checked by: Magnum Fan

Date: 17/09/2012

High-Volume TSP Sampler  
5-Point Calibration Record9

Location : AM6  
Calibrated by : P.F.Yeung  
Date : 20/09/2012

Sampler

Model : GMWS-2310 ACCU-VOL  
Serial Number : S/N 1254

Calibration Office and Standard Calibration Relationship

Serial Number : 1378  
Service Date : 22 Feb 2012  
Slope (m) : 1.99405  
Intercept (b) : -0.00397  
Correlation Coefficient(r) : 0.99984

Standard Condition

Pstd (hpa) : 1013  
Tstd (K) : 298.18

Calibration Condition

Pa (hpa) : 1011  
Ta(K) : 300

Resistance Plate	dH [green liquid] (inch water)	Z	X=Qstd (cubic meter/min)	IC	Y
1   18 holes	9.2	3.011	1.512	64	63.5
2   13 holes	7.1	2.645	1.328	55	54.6
3   10 holes	5.8	2.390	1.201	48	47.6
4   7 holes	3.7	1.909	0.959	37	36.7
5   5 holes	2.2	1.472	0.740	26	25.8

Sampler Calibration Relationship

Slope(m):47.352 Intercept(b): -7.425 Correlation Coefficient(r): 0.9999

Checked by: Magnum Fan

Date: 24/09/2012

# Certificate of Calibration

## 校正證書

Certificate No. : C124191  
證書編號

### ITEM TESTED / 送檢項目 ( Job No. / 序引編號 : IC12-1770 )

Description / 儀器名稱 : Sound Level Meter  
Manufacturer / 製造商 : Rion  
Model No. / 型號 : NL-31  
Serial No. / 編號 : 00603867  
Supplied By / 委託者 : Envirotech Services Co.  
Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,  
Hong Kong

### TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$       Relative Humidity / 相對濕度 :  $(55 \pm 20)\%$   
Line Voltage / 電壓 : ---

### TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 18 July 2012


### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
All results are within manufacturer's specification.  
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies, USA
- Fluke Everett Service Center, USA
- Fluke Precision Measurement Ltd., UK
- Rohde & Schwarz Laboratory, Germany

Tested By :   
測試 : \_\_\_\_\_  
L K Yeung

Certified By :   
核證 : \_\_\_\_\_  
K C Lee

Date of Issue : 18 July 2012  
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C124191  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL280	40 MHz Arbitrary Waveform Generator	C120016
CL281	Multifunction Acoustic Calibrator	DC110233

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.8	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.8 (Ref.)
				104.00		103.8
				114.00		113.8

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.8	Ref.
			Slow			93.7	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C124191  
證書編號

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L <sub>A</sub>	A	Fast	94.00	63 Hz	67.6	-26.2 ± 1.5
					125 Hz	77.6	-16.1 ± 1.5
					250 Hz	85.1	-8.6 ± 1.4
					500 Hz	90.6	-3.2 ± 1.4
					1 kHz	93.8	Ref.
					2 kHz	95.1	+1.2 ± 1.6
					4 kHz	95.0	+1.0 ± 1.6
					8 kHz	92.8	-1.1 (+2.1 ; -3.1)
					12.5 kHz	89.9	-4.3 (+3.0 ; -6.0)

#### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L <sub>C</sub>	C	Fast	94.00	63 Hz	93.0	-0.8 ± 1.5
					125 Hz	93.6	-0.2 ± 1.5
					250 Hz	93.8	0.0 ± 1.4
					500 Hz	93.9	0.0 ± 1.4
					1 kHz	93.9	Ref.
					2 kHz	93.7	-0.2 ± 1.6
					4 kHz	93.2	-0.8 ± 1.6
					8 kHz	90.9	-3.0 (+2.1 ; -3.1)
					12.5 kHz	88.1	-6.2 (+3.0 ; -6.0)

Remarks : - Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz : ± 0.35 dB  
 250 Hz - 500 Hz : ± 0.30 dB  
 1 kHz : ± 0.20 dB  
 2 kHz - 4 kHz : ± 0.35 dB  
 8 kHz : ± 0.45 dB  
 12.5 kHz : ± 0.70 dB  
 104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)  
 114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

#### Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606

Fax/傳真: 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com





# Certificate of Calibration

## 校正證書

Certificate No. : C123580  
 證書編號

**ITEM TESTED / 送檢項目 ( Job No. / 序引|編號 : IC12-1472 )**

Description / 儀器名稱 : Sound Level Meter  
 Manufacturer / 製造商 : Rion  
 Model No. / 型號 : NL-31  
 Serial No. / 編號 : 00410224  
 Supplied By / 委託者 : Envirotech Services Co.  
 Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,  
 Hong Kong

**TEST CONDITIONS / 測試條件**

Temperature / 溫度 : (23 ± 2)°C  
 Relative Humidity / 相對濕度 : (55 ± 20)%  
 Line Voltage / 電壓 : ---

**TEST SPECIFICATIONS / 測試規範**

Calibration check

**DATE OF TEST / 測試日期** : 15 June 2012


**TEST RESULTS / 測試結果**

The results apply to the particular unit-under-test only.  
 All results are within manufacturer's specification.  
 The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Precision Measurement Ltd., UK
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By :   
 測試 : L K Yeung

Certified By :   
 核證 : K C Lee

Date of Issue : 15 June 2012  
 簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C123580  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C120016
CL281	Multifunction Acoustic Calibrator	DC110233

- Test procedure : MA101N.

- Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.7	± 1.1

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.7 (Ref.)
				104.00		103.7
				114.00		113.7

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

- 6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.7	Ref.
			Slow			93.6	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C123580  
證書編號

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L <sub>A</sub>	A	Fast	94.00	63 Hz	67.3	-26.2 ± 1.5
					125 Hz	77.4	-16.1 ± 1.5
					250 Hz	85.0	-8.6 ± 1.4
					500 Hz	90.4	-3.2 ± 1.4
					1 kHz	93.7	Ref.
					2 kHz	95.0	+1.2 ± 1.6
					4 kHz	94.8	+1.0 ± 1.6
					8 kHz	92.7	-1.1 (+2.1 ; -3.1)
					12.5 kHz	89.8	-4.3 (+3.0 ; -6.0)

#### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L <sub>C</sub>	C	Fast	94.00	63 Hz	92.8	-0.8 ± 1.5
					125 Hz	93.5	-0.2 ± 1.5
					250 Hz	93.7	0.0 ± 1.4
					500 Hz	93.8	0.0 ± 1.4
					1 kHz	93.7	Ref.
					2 kHz	93.6	-0.2 ± 1.6
					4 kHz	93.1	-0.8 ± 1.6
					8 kHz	90.8	-3.0 (+2.1 ; -3.1)
					12.5 kHz	88.0	-6.2 (+3.0 ; -6.0)

Remarks : - Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz : ± 0.35 dB  
 250 Hz - 500 Hz : ± 0.30 dB  
 1 kHz : ± 0.20 dB  
 2 kHz - 4 kHz : ± 0.35 dB  
 8 kHz : ± 0.45 dB  
 12.5 kHz : ± 0.70 dB  
 104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)  
 114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

#### Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C124011  
證書編號

### ITEM TESTED / 送檢項目 ( Job No. / 序引編號 : IC12-1674 )

Description / 儀器名稱 : Sound Level Calibrator  
Manufacturer / 製造商 : Rion  
Model No. / 型號 : NC-73  
Serial No. / 編號 : 10997142  
Supplied By / 委託者 : Envirotech Services Co.  
Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,  
Hong Kong

### TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$       Relative Humidity / 相對濕度 :  $(55 \pm 20)\%$   
Line Voltage / 電壓 : ---

### TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 9 July 2012

### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
All results are within manufacturer's specification.  
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By :   
測試 : L K Yeung

Certified By :   
核證 : K C Lee

Date of Issue : 10 July 2012  
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C124011  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C123541
CL281	Multifunction Acoustic Calibrator	DC110233
TST150A	Measuring Amplifier	C120886

- Test procedure : MA100N.

- Results :

### 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.5	± 0.2

### 5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	0.990	1 kHz ± 2 %	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

### Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



## RION CO., LTD.

3-20-41 Higashimotomachi Kokubunji Tokyo 185-8533  
Phone:042(359)7888, Facsimile:042(359)7442

# Certificate of Calibration

**Name** : Precision sound level meter  
**Model** : NL-52 S/No. : 00710259  
( NX-42EX installed )  
**Microphone** : UC-59 S/No. : 02695  
**Preamplifier** : NH-25 S/No. : 10253

**Date of Calibration** : September, 20, 2011

We hereby certify that the above product was tested and calibrated according to the prescribed Rion procedures, and that it fulfills specification requirements.

The measuring equipment and reference devices used for testing and calibrating this unit are managed under the Rion traceability system and are traceable according to official Japanese standards and official standards of countries belonging to the International Committee of Weights and Measures.

  
RION CO., LTD.

*T. Kano*  
Manager, Quality Control Department



# Certificate of Calibration

## 校正證書

Certificate No. : C124184  
證書編號

**ITEM TESTED / 送檢項目 ( Job No. / 序引編號 : IC12-1770 )**

Description / 儀器名稱 : Sound Level Calibrator  
 Manufacturer / 製造商 : Rion  
 Model No. / 型號 : NC-73  
 Serial No. / 編號 : 10786708  
 Supplied By / 委託者 : Envirotech Services Co.  
 Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,  
 Hong Kong

**TEST CONDITIONS / 測試條件**

Temperature / 溫度 : (23 ± 2)°C  
 Relative Humidity / 相對濕度 : (55 ± 20)%  
 Line Voltage / 電壓 : ---

**TEST SPECIFICATIONS / 測試規範**

Calibration check


**DATE OF TEST / 測試日期** : 17 July 2012

**TEST RESULTS / 測試結果**

The results apply to the particular unit-under-test only.  
 All results are within manufacturer's specification.  
 The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies, USA
- Fluke Everett Service Center, USA
- Rohde & Schwarz Laboratory, Germany

Tested By :   
 測試 : L K Yeung

Certified By :   
 核證 : K C Lee

Date of Issue : 18 July 2012  
 簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C124184  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C123541
CL281	Multifunction Acoustic Calibrator	DC110233
TST150A	Measuring Amplifier	C120886

- Test procedure : MA100N.

- Results :

### 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	93.9	± 0.5	± 0.2

### 5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	0.990	1 kHz ± 2 %	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

#### Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.





TISCH ENVIRONMENTAL, INC.  
 145 SOUTH MIAMI AVE.  
 VILLAGE OF CLEVELAND, OH 45002  
 513.467.9000  
 877.263.7610 TOLL FREE  
 513.467.9009 FAX  
 WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Feb 22, 2012 Rootsmeter S/N 0438320 Ta (K) - 295  
 Operator Tisch Orifice I.D. - 1378 Pa (mm) - 740.41

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.3940	3.2	2.00
2	NA	NA	1.00	0.9740	6.4	4.00
3	NA	NA	1.00	0.8720	8.0	5.00
4	NA	NA	1.00	0.8340	8.8	5.50
5	NA	NA	1.00	0.6870	12.8	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9799	0.7029	1.4029	0.9957	0.7142	0.8927
0.9756	1.0017	1.9841	0.9914	1.0178	1.2624
0.9734	1.1163	2.2183	0.9891	1.1343	1.4114
0.9724	1.1660	2.3265	0.9881	1.1848	1.4803
0.9671	1.4077	2.8059	0.9827	1.4304	1.7853
Qstd slope (m) = 1.99405			Qa slope (m) = 1.24864		
intercept (b) = -0.00397			intercept (b) = -0.00252		
coefficient (r) = 0.99984			coefficient (r) = 0.99984		
y axis = SQRT[H2O(Pa/760)(298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

$V_{std} = \text{Diff. Vol} [(Pa - \text{Diff. Hg}) / 760] (298 / Ta)$   
 $Q_{std} = V_{std} / \text{Time}$

$V_a = \text{Diff Vol} [(Pa - \text{Diff Hg}) / Pa]$   
 $Q_a = V_a / \text{Time}$

For subsequent flow rate calculations:

$Q_{std} = 1/m \{ [\text{SQRT} (H_2O (Pa/760) (298/Ta))] - b \}$   
 $Q_a = 1/m \{ [\text{SQRT} H_2O (Ta/Pa)] - b \}$

Annex I

Event / Action Plans for Air  
Quality, Noise and  
Landscape and Visual  
Monitoring

**Table I1**      *Event Action Plan for Air Quality Monitoring*

<b>Action Level/Limit Level</b>	<b>Environmental Team Leader (ETL)</b>	<b>Independent Environmental Checker (IEC)</b>	<b>Engineer's Representative (ER)</b>	<b>Contractor</b>
<i>Action Level</i>				
Exceedance for one sample	<ul style="list-style-type: none"> <li>• Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>• Inform IEC and ER;</li> <li>• Repeat measurement to confirm finding; and,</li> <li>• Increase monitoring frequency to daily.</li> </ul>	<ul style="list-style-type: none"> <li>• Check monitoring data submitted by ET; and,</li> <li>• Check Contractor's working method.</li> </ul>	<ul style="list-style-type: none"> <li>• Notify Contractor</li> </ul>	<ul style="list-style-type: none"> <li>• Rectify any unacceptable practice; and,</li> <li>• Amend working methods if appropriate.</li> </ul>
Exceedance for two or more consecutive samples	<ul style="list-style-type: none"> <li>• Identify source;</li> <li>• Inform IEC and ER;</li> <li>• Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>• Repeat measurements to confirm findings;</li> <li>• Increase monitoring frequency to daily; and,</li> <li>• Discuss with IEC and Contractor on remedial actions required;</li> </ul>	<ul style="list-style-type: none"> <li>• Check monitoring data submitted by ET;</li> <li>• Check Contractor's working method;</li> <li>• Discuss with ET and Contractor on possible remedial measures;</li> <li>• Advise the ET on the effectiveness of the proposed remedial measures; and,</li> <li>• Supervise Implementation of remedial measures.</li> </ul>	<ul style="list-style-type: none"> <li>• Confirm receipt of notification of failure in writing;</li> <li>• Notify Contractor, and,</li> <li>• Ensure remedial measures properly implemented.</li> </ul>	<ul style="list-style-type: none"> <li>• Submit proposals for remedial to ER within 3 working days of notification;</li> <li>• Implement the agreed proposals;</li> <li>• Amend proposal if appropriate.</li> </ul>

Action Level/Limit Level	Environmental Team Leader (ETL)	Independent Environmental Checker (IEC)	Engineer's Representative (ER)	Contractor
<i>Limit Level</i>				
Exceedance for one sample	<ul style="list-style-type: none"> <li>Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>Inform ER, Contractor and EPD;</li> <li>Repeat measurement to confirm finding;</li> <li>Increase monitoring frequency to daily; and,</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> </ul>	<ul style="list-style-type: none"> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with ET and Contractor on possible remedial measures;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures; and,</li> <li>Supervise implementation of remedial measures.</li> </ul>	<ul style="list-style-type: none"> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor; and,</li> <li>Ensure remedial measures properly implemented.</li> </ul>	<ul style="list-style-type: none"> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals; and,</li> <li>Amend proposal if appropriate.</li> </ul>
Exceedance for two or more consecutive samples	<ul style="list-style-type: none"> <li>Notify IEC, ER, Contractor and EPD;</li> <li>Identify source;</li> <li>Repeat measurement to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and,</li> <li>If exceedance stops, cease additional monitoring.</li> </ul>	<ul style="list-style-type: none"> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and,</li> <li>Supervise the implementation of remedial measures.</li> </ul>	<ul style="list-style-type: none"> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Ensure remedial measures properly implemented; and,</li> <li>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ul>	<ul style="list-style-type: none"> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Resubmit proposals if problem still not under control; and,</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ul>

**Table I2** *Event Action Plan for Noise Monitoring*

Action Level/Limit Level	Environmental Team Leader (ETL)	Independent Environmental Checker (IEC)	Engineer's Representative (ER)	Contractor
Action Level being exceeded	<ul style="list-style-type: none"> <li>Notify ER, IEC and Contractor;</li> <li>Carry out investigation;</li> <li>Report the results of investigation to the IEC, ER and Contractor;</li> <li>Discuss with the IEC and Contractor on remedial measures required; and,</li> <li>Increase monitoring frequency to check mitigation effectiveness.</li> </ul>	<ul style="list-style-type: none"> <li>Review the investigation results submitted by the ET;</li> <li>Review the proposed remedial measures by the Contractor and advise the ER accordingly; and,</li> <li>Advise the ER on the effectiveness of the proposed remedial measures.</li> </ul>	<ul style="list-style-type: none"> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; and,</li> <li>Supervise the implementation of remedial measures.</li> </ul>	<ul style="list-style-type: none"> <li>Submit noise mitigation proposals to IEC and ER; and,</li> <li>Implement noise mitigation proposals.</li> </ul>

Action Level/Limit Level	Environmental Team Leader (ETL)	Independent Environmental Checker (IEC)	Engineer's Representative (ER)	Contractor
Limit Level being exceeded	<ul style="list-style-type: none"> <li>• Inform IEC, ER, Contractor and EPD;</li> <li>• Repeat measurements to confirm findings;</li> <li>• Increase monitoring frequency;</li> <li>• Identify source and investigate the cause of exceedance;</li> <li>• Carry out analysis of Contractor's working procedures;</li> <li>• Discuss with the IEC, Contractor and ER on remedial measures required;</li> <li>• Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and,</li> <li>• If exceedance stops, cease additional monitoring.</li> </ul>	<ul style="list-style-type: none"> <li>• Discuss amongst ER, ET, and Contractor on the potential remedial actions; and,</li> <li>• Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.</li> </ul>	<ul style="list-style-type: none"> <li>• Confirm receipt of notification of failure in writing;</li> <li>• Notify Contractor;</li> <li>• In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>• Supervise the implementation of remedial measures; and,</li> <li>• If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.</li> </ul>	<ul style="list-style-type: none"> <li>• Take immediate action to avoid further exceedance;</li> <li>• Submit proposals for remedial actions to IEC and ER within 3 working days of notification;</li> <li>• Implement the agreed proposals;</li> <li>• Submit further proposal if problem still not under control; and,</li> <li>• Stop the relevant portion of works as instructed by the ER until the exceedance is abated.</li> </ul>

**Table I3** *Event and Action Plan for Landscape and Visual Impact - Construction Phase*

<b>Action Level</b>	<b>Environmental Team Leader (ETL)</b>	<b>Independent Environmental Checker (IEC)</b>	<b>Engineer's Representative (ER)</b>	<b>Contractor</b>
Non-conformity on one occasion	Identify source Inform the IEC and the ER Discuss remedial actions with the IEC, the ER and the Contractor Monitor remedial action until rectification has been completed	Check report Check the Contractor's working method Discuss with the ER and the Contractor on possible remedial measures Advise the ER on effectiveness of proposed remedial measures	Notify the Contractor Ensure remedial measures are properly implemented	Amend working methods Rectify damage and undertake remedial measures or any necessary replacement
Repeated Non-conformity	Identify source Inform the IEC and the ER Increase monitoring (site audit) frequency Discuss remedial actions with the IEC, the ER and the Contractor Monitor remedial actions until rectification has been completed If exceedance stops, cease additional monitoring (site audit)	Check report Check the Contractor's working method Discuss with the ER and the Contractor on possible remedial measures Advise the ER on effectiveness of proposed remedial measures Supervise implementation of remedial measures	Notify the Contractor Ensure remedial measures are properly implemented	Amend working methods Rectify damage and undertake remedial measures or any necessary replacement

Annex J

## Waste Flow Table



# Harbour Area Treatment Scheme Stage 2A – Construction of Sewage Conveyance System from North Point to Stonecutters Island

**Contract No. : DC/2007/23**

## Monthly Summary Waste Flow Table for 2009 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Concrete (see Note 4)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Metals (see Note 2)	Paper/ cardboard packaging (see Note 2)	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000kg)	(in '000kg)	(in '000kg)	(in'000kg / '000L)	(in '000m <sup>3</sup> )
Jan										
Feb										
Mar										
Apr										
May										
June										
<b>Sub-total</b>										
July	0	0	0	0	0	0	0	0	0	0
Aug	0	0	0	0	0	0	0	0	0	0
Sept	0.016	0	0	0	Dry	Wet	0	0	0	0.068
					0.016	0				
Oct	0.523	0	0	0	0.523	0	0	0	0	0.086
Nov	2.331	0	0	0	2.275	0.056	99.2	0.036	0	0.129
Dec	3.803	0	0	0	3.004	0.799	1	0	0	0.120
<b>Total</b>	<b>6.673</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>5.818</b>	<b>0.855</b>	<b>100.2</b>	<b>0.036</b>	<b>0</b>	<b>0.403</b>

- Notes:
- (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  - (2) Metal and paper/cardboard packaging will be collected by recycler for recycling.
  - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material and the wastes are collected by recycler for recycling.
  - (4) Broken concrete for recycling into aggregates
  - (5) If necessary, use the conversion factor: 1 full load of dumping truck being equivalent to 6.5 m<sup>3</sup> by volume.
  - (6) For chemical waste, the actual quantities of empty paint cans will be in kilogram (kg) and spent lubrication oil will be in litre (L).

Harbour Area Treatment Scheme Stage 2A – Construction of Sewage Conveyance System from North Point to Stonecutters Island  
**Contract No. : DC/2007/23**  
**Monthly Summary Waste Flow Table for 2010 (year)**

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Concrete (see Note 4)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill		Metals (see Note 2)	Paper/ cardboard packaging (see Note 2)	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )		(in '000kg)	(in '000kg)	(in '000kg)	(in'000kg / '000L)	(in '000m <sup>3</sup> )
Jan	5.341	0	0	0	Dry 3.066	Wet 2.275	0	0.144	0	0.8	0.178
Feb	3.328	0	0	0	1.541	1.787	0	0	0	0	0.167
Mar	4.486	0	0	0	2.019	2.467	0	0.09	0	0	0.148
Apr	4.864	0	0	0	1.756	3.108	0	0.054	0	0	0.160
May	7.092	0	0	0	3.383	3.709	0	0.144	0	0.3	0.157
June	6.190	0	0	0	1.083	5.107	0	0.09	0	0.4	0.455
<b>Sub-total</b>	<b>31.301</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>12.848</b>	<b>18.453</b>	<b>0</b>	<b>0.522</b>	<b>0</b>	<b>1.5</b>	<b>1.265</b>
July	5.031	0	0	0	1.006	4.025	0	0.162	0	0	0.212
Aug	5.140	0	0	0.23	1.970	2.940	0	0.09	0	0.4	0.312
Sept	3.593	0.15	0	0.35	1.771	1.322	0	0.09	0	1	0.146
Oct	2.324	0	0	0	1.429	0.895	0	0.144	0	0	0.078
Nov	5.927	0	0	0	4.383	1.544	0	0	0	0.8	0.078
Dec	4.963	0	0	0	4.840	0.123	0	0.072	0	0	0.078
<b>Total</b>	<b>58.279</b>	<b>0.15</b>	<b>0</b>	<b>0.58</b>	<b>28.247</b>	<b>29.302</b>	<b>0</b>	<b>1.080</b>	<b>0</b>	<b>3.7</b>	<b>2.169</b>

- Notes:
- (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  - (2) Metal and paper/cardboard packaging will be collected by recycler for recycling.
  - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material and the wastes are collected by recycler for recycling.
  - (4) Broken concrete for recycling into aggregates
  - (5) If necessary, use the conversion factor: 1 full load of dumping truck being equivalent to 6.5 m<sup>3</sup> by volume.
  - (6) For chemical waste, the actual quantities of empty paint cans will be in kilogram (kg) and spent lubrication oil will be in litre (L).

Harbour Area Treatment Scheme Stage 2A – Construction of Sewage Conveyance System from North Point to Stonecutters Island  
**Contract No. : DC/2007/23**  
**Monthly Summary Waste Flow Table for 2011 (year)**

Month	Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of C&D Wastes Generated Monthly					
	Total Quantity Generated	Broken Concrete (see Note 4)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill		Metals (see Note 2)	Paper/ cardboard packaging (see Note 2)	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )		(in '000kg)	(in '000kg)	(in '000kg)	(in'000kg / '000L)	(in '000m <sup>3</sup> )
Jan	8.423	0	0	0	Dry	Wet	0	0.09	0	1.2	0.124
					8.236	0.187					
Feb	7.794	0	0	0.799	6.814	0.181	0	0.09	0	0	0.138
Mar	9.641	0	0	0.576	9.007	0.058	0	0.19	0	0	0.059
Apr	8.841	0	0	2.014	6.730	0.097	0	0.09	0	0.2	0.069
May	5.416	0	0	0.887	4.280	0.249	0	0.09	0	0	0.077
June	7.507	0	0	0.665	6.245	0.597	0	0.337	0.028	1.0	0.072
Sub-total	47.622	0	0	4.941	41.312	1.369	0	0.887	0.028	2.4	0.539
July	5.31	0	0	2.372	2.795	0.143	0	0.162	0	0	0.109
Aug	5.381	0	0	2.553	2.530	0.298	0	0.248	0.035	0.4	0.097
Sept	6.963	0	0	2.814	3.974	0.175	0	0.289	0.032	0	0.155
Oct	5.330	0	0	0.794	4.385	0.151	0	0.254	0.015	0	0.128
Nov	5.009	0	0	0.995	3.760	0.254	0	0.270	0	0.6	0.116
Dec	5.429	0	0.159	1.430	3.522	0.318	0	0.216	0	0	0.117
Total	81.044	0	0.159	15.899	62.278	2.708	0	2.326	0.11	3.4	1.261

- Notes:
- (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  - (2) Metal and paper/cardboard packaging will be collected by recycler for recycling.
  - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material and the wastes are collected by recycler for recycling.
  - (4) Broken concrete for recycling into aggregates
  - (5) If necessary, use the conversion factor: 1 full load of dumping truck being equivalent to 6.5 m<sup>3</sup> by volume.
  - (6) For chemical waste, the actual quantities of empty paint cans will be in kilogram (kg) and spent lubrication oil will be in litre (L).

# Harbour Area Treatment Scheme Stage 2A – Construction of Sewage Conveyance System from North Point to Stonecutters Island

**Contract No. : DC/2007/23**

## Monthly Summary Waste Flow Table for 2012 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Concrete (see Note 4)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill		Metals (see Note 2)	Paper/ cardboard packaging (see Note 2)	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )		(in '000kg)	(in '000kg)	(in '000kg)	(in'000kg / '000L)	(in '000m <sup>3</sup> )
Jan	6,208	0	0	1.615	Dry	Wet	0	0.108	0	0.4	0.117
					4.277	0.316					
Feb	6.006	0	0	0.443	5.148	0.415	0	0.108	0	0	0.063
Mar	8.370	0	0	1.226	6.871	0.273	0	0.108	0	0	0.181
Apr	8.899	0	0	1.101	7.581	0.217	0	0.036	0	0	0.685
May	6.789	0	0	0.716	5.931	0.142	0	0.108	0	0.4	0.103
June	7.585	0	0.021	5.565	1.789	0.213	0.014	0.256	0	0.0	0.197
Sub-total	43.857	0	0.021	10.666	31.594	1.576	0.014	0.724	0	0.8	1.346
July	9.128	0	0	5.240	3.730	0.158	8.356	0.055	0	0.8	0.171
Aug	5.756	0	0	3.836	1.640	0.280	0.008	0.062	0	0.2	0.126
Sept	7.809	0	0.172	2.103	5.062	0.472	0.007	0.172	0	0.4	0.105
Oct											
Nov											
Dec											
Total	66.55	0	0.193	21.845	42.026	2.486	8.385	1.813	0	2.2	1.748

- Notes:
- (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  - (2) Metal and paper/cardboard packaging will be collected by recycler for recycling.
  - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material and the wastes are collected by recycler for recycling.
  - (4) Broken concrete for recycling into aggregates
  - (5) If necessary, use the conversion factor: 1 full load of dumping truck being equivalent to 6.5 m<sup>3</sup> by volume.
  - (6) For chemical waste, the actual quantities of empty paint cans will be in kilogram (kg) and spent lubrication oil will be in litre (L).
