Fugro Development Centre, 5 Lok Yi Street, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852 2450 8233 Fax : +852 2450 6138 E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk



Ref No.: 100440EN121502

Contract No. EP/SP/58/08

Sludge Treatment Facilities

Quarterly Environmental Monitoring and Audit Report
For

September 2012 to November 2012

Report No.: 1004

100440EN121502

Certified by

John K. M. Ho (Environmental Team Leader)

Date

.

20 December 2012

Fugro Development Centre,

5 Lok Yi Street, Tai Lam,

Tuen Mun, N.T.,

Hong Kong.

Tel: +852-2450 8233

Fax: +852-2450 6138

E-mail: matlab@fugro.com.hk

Website: www.materialab.com.hk



Ref No.: 100440EN121502

CONTENTS

Figure (4.1 - 4.2)

CONTENTS	
1.	Executive Summary
2.	Introduction
3.	General Review
4.	Construction Phase Environmental Monitoring and Audit
5.	Summary of Complaints, Summons and Successful Prosecutions
6.	Comments and Conclusions for September 2012 to November 2012
Appendices:	
Appendix 1:	Environmental Mitigation Implementation Schedule
Appendix 2:	Graphical Presentation of Water Quality Monitoring Data
Appendix 3:	Summary of Ecology Monitoring
Appendix 4:	Summary of Landscape and Visual Impact Survey
Appendix 5:	Summary of Waste Flow
Appendix 6:	Event / Action Plan for Water Quality
Appendix 7:	Figures
Appendix 8:	Work Program
List of Tables:	
Table 3.1	Summary of Monitored Parameters
Table 3.2	Action and Limit Level for Water Quality
Table 3.3	Action Level for Landfill Gas Measurement
Table 4.1	Summary of Environmental Monitoring from September 2012 to November 2012
Table 4.2	Summary of Landfill Gas Monitoring
Table 4.3	Construction Activity Undertaken during September 2012 to November 2012
Table 4.4	Summary of Monitoring Non-Compliances
Table 4.5	Summary of Reasons for the Exceedances of Water Quality
Table 5.1	Summary of Environmental Complaints and Prosecutions
List of Figures:	
Figure 1.1	WENT Landfill Control Zone
Figure 3.1	Location of Project Site
Figure 3.2	Project Organisation Structure

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

Water Quality Monitoring Location

Fugro Development Centre,

5 Lok Yi Street, Tai Lam,

Tuen Mun, N.T.,

Hong Kong.

Tel: +852-2450 8233

Fax: +852-2450 6138

E-mail: matlab@fugro.com.hk

Website: www.materialab.com.hk



Ref No.: 100440EN121502

1. Executive Summary

The requisite construction works for the Environmental Protection Department Contract No. EP/SP/58/08 Sludge Treatment has commenced construction activity on 22 December 2010. The requisite impact environmental monitoring comprising of water quality, landfill gas, ecology, landscape and visual impact was conducted throughout this reporting quarter.

Air Quality and Noise Level

Accordance to EIA study, there is no sensitive receiver for air and noise located nears the construction area and hence dust and noise monitoring is not required.

Stream Water Quality

1 non-compliance event regarding pH was recorded in the past three months.

Marine Water Quality

Piling work was commenced on 21 February 2011 and the foundation piling work was completed on 13 October 2011. The pre-bore piling of the STF was completed on 22 February 2012 and the post monitoring for marine water has been completed on 20 March 2012. Although marine water quality monitoring resumed on 03 July 2012 due to the commencement of pre-bore operation for sheet piling, the pre-bore operation as planned was not carry out. Therefore the impact marine water quality monitoring was suspended on 20 August 2012 and post impact monitoring is not required.

Landfill Gas Monitoring

Excavation works has been carried out within the WENT landfill consultation zone in the reporting period. Landfill gas monitoring was carried out by a competent person during the excavation, operation in chamber and confined space within the WENT landfill control zone and no exceedance was found.

Ecology

Routine ecology monitoring was carried out throughout the reporting quarter.

Landscape and Visual Monitoring

Monitoring of landscape and visual impact was conducted to ensure compliance with the intended aims of the measures and the effectiveness of the mitigation measures.

Complaints

As far as the complaint on the construction work in respect of environmental protection and pollution control was concerned, there was no complaint received during this reporting quarter.

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company,

Fugro Development Centre,

5 Lok Yi Street, Tai Lam,

Tuen Mun, N.T.,

Hong Kong.

Tel: +852-2450 8233

Fax: +852-2450 6138

E-mail: matlab@fugro.com.hk

Website: www.materialab.com.hk



Ref No.: 100440EN121502

2. Introduction

This quarterly report reviews the progress of the environmental monitoring and audit work associated with Contract No. EP/SP/58/08 Sludge Treatment Facilities in Nim Wan for the eighth quarter of construction activity from 25 August 2012 to 24 November 2012.

The graphical plots of the monitoring data are presented in Appendix 2.

Summary of ecology monitoring, landscape and visual impact monitoring are attached in Appendix 3 and 4 respectively. Comments and conclusions for this reporting quarter are included.

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel: +852-2450 8233
: +852-2450 6138
: matlab@fugro.com.hk
: matlab@fugro.com.hk



Ref No.: 100440EN121502

3. General Review

3.1 Background

The Contractor, VW-VES (HK) Limited, has been awarded a contract by the Environmental Protection Department of the Government of the Hong Kong Special Administrative Region for the Sludge Treatment Facilities. The location of the site is shown in Figure 3.1.

The program commenced in November 2010 and is anticipated to complete in 2013.

The construction schedule will be based on the major works associated with the project. The major works under this contract include:

Incineration Plant

- a) Sludge receiving, storage and feeding system
- b) Fluidized bed incinerators
- c) Waste heat recovery and power generation system
- d) Flue gas treatment system
- e) Ash storage and handling system
- f) Residue storage and handling system
- g) Fluidized bed sand storage and handing system
- h) Reagent reception and storage system
- i) Process control and monitoring system

Ancillary and Supporting Facilities

- a) Weighbridge
- b) Site security
- c) Administration building
- d) Vehicle washing facilities
- e) Maintenance workshop and utility yard
- f) Drainage system
- g) Sewerage system
- h) Sewage treatment works
- i) Water supply system
- j) Deodorization system

The project organisation with respect to environmental protection works is shown in Figure 3.2, which indicates responsibilities and lines of communication of the various parties concerned.

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel: +852-2450 8233
: +852-2450 6138
: matlab@fugro.com.hk
Uvebsite: www.materialab.com.hk



Ref No.: 100440EN121502

3.2 Summary of Environmental Monitoring and Audit (EM&A) Requirements

The EM&A program requires the monitoring of water quality prior to the commencement of and during the construction. A baseline report was prepared in December 2010 for the contract based on monitoring data acquired before the commencement of construction works.

Impact monitoring of water quality is to be undertaken at the designated monitoring stations. The monitored parameters are summarized in Table 3.1.

Action and Limit (AL) levels are established based on the data from the baseline report. Should the monitoring results indicate any non-compliance of AL levels, actions according to the Event / Action Plan in Appendix 6 are to be followed and appropriate environmental mitigation measures as in Appendix 1 are to be implemented to rectify the situation. The implementation status of mitigation measures is also shown in Appendix 1.

Impact ecology and visual survey monitoring are to be conducted at the construction area on regular basis. Monitoring parameters are tabulated in Table 3.1.

Landfill gas monitoring is required whenever there is excavation deeper than 300mm or works conducted in confined space within the WENT Landfill Consultation Zone (see Figure 1.1).

The Contractors (VW-VES (HK) Limited) is responsible for waste control within the construction site, removal of the waste material produced from the site and to implement any mitigation measures to minimize waste or redress problems arising from the waste from the site. The waste material may include any sewage, waste water or effluent containing sand, cement, silt or any other suspended or dissolved material to flow from the site onto any adjoining land, storm sewer, sanitary water, or any waste matter or refuse to be deposited anywhere within the site or onto any adjoining land.

The Contractor shall also pay attention to the Waste Disposal Ordinance, the Dumping at Sea Ordinance, the Public Health and Municipal Services Ordinance and the Water Pollution Control Ordinance, and carry out the appropriate waste management work. The relevant licence / permit, such as the effluent discharge licence, the chemical waste producer registration, etc. shall be obtained. The Contractor shall refer to the relevant booklets issued by EPD when applying for the licence / permit.

The environmental mitigation measures and status for waste management are summarized in Appendix 1.

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

Fugro Development Centre, Tel: +852-2450 8233
5 Lok Yi Street, Tai Lam, Fax: +852-2450 6138
Tuen Mun, N.T., E-mail: matlab@fugro.com.hk
Hong Kong. Website: www.materialab.com.hk



Ref No.: 100440EN121502

Table 3.1 Summary of Monitored Parameters

	Table 3.1 Summary of Monitored Parameters						
Parameters	Monitored Items	Number of Stations	Frequency	Requirement			
Marine water	CadmiumChromiumAluminium	2 monitoring stations and 1 control station	Three days per week for mid-ebb and mid-flood tides during foundation piling of the STF	Sampling is taken at three water depths, namely, 1m below water Surface, middepth and 1m above sea bed, except where the water depth be less than 6m, in which case the middepth station may be omitted. Shall the water depth be less than 3m, only the mid-depth station will be monitored.			
Stream water	 pH Turbidity Suspended solids Dissolved oxygen 	3 monitoring stations and 2 control stations	Three days per week for mid-ebb and mid-flood tides during site formation and foundation piling of the STF and construction of the access road	 Two consecutive measurements of DO concentration, DO saturation, turbidity and pH are taken at middepth at each location. Water samples for SS measurement is collected at the same depth at each location. 			
Ecology	Site condition and bird monitoring	Whole Middle Lagoon and 20m from the boundary of the Lagoon	 Monthly monitoring for avifauna Habitat monitoring at least twice per month Monthly vegetation monitoring 	 Avifauna and their behavior. All birds seen and heard should be identified and counted. Signs of breeding of birds. Coverage of water and PFA filling activities in Middle Lagoon. 			
Landscape and Visual Impact	All measures, including compensatory planting, undertaken by both the Contractor and the specialist Landscape Sub-Contractor	East Lagoon	Biweekly	Ensure compliance with the intended aims of the measures and the effectiveness of the mitigation measures.			

Fugro Development Centre, Tel : +852-2450 8233 5 Lok Yi Street, Tai Lam, Fax : +852-2450 6138 Tuen Mun, N.T., E-mail : matlab@fugro.com.hk Hong Kong. Website : www.materialab.com.hk



Ref No.: 100440EN121502

Table 3.1 (Con't)

Parameters	Monitored	Number of	Frequency	Requirement
	Items	Stations		•
Landfill gas	 Oxygen Methane Carbon dioxide 	Excavation, operation in chamber and confined space within the WENT Landfill Control Zone. (See Figure 1.1)	During the construction and operation	 Excavation between 300mm to 1m deep: Directly after the excavation has been completed. Periodically whilst the excavation remains open. Excavation deeper than 1m: At ground surface before excavations commences. Immediately before any worker enters the excavation. At the beginning of each working day for the entire period the excavation remains open. Periodically whilst the excavation remains open.

3.3 Action and Limit Levels

Water Quality Limit

Environmental auditing on the monitoring data is to be undertaken based on the Action and Limit (AL) levels for water quality to check against any non-compliances.

The AL levels for monitored parameters are formulated from the baseline monitoring data. The AL levels for marine and stream water quality are tabulated in Table 3.2.

Table 3.2 Action and Limit Levels for Marine and Stream Water Quality

Parameters	Action Level	Limit Level
DO in mg/L	≤ 5.16	≤ 4
(mid-depth)		
SS in mg/L	≥ 41 <u>AND</u> 120% of control	≥ 85 <u>AND</u> 130% of control
(mid-depth)	station's SS on the same day	station's SS on the same day
	of measurement	of measurement
Turbidity in NTU	≥ 36.4 AND 120% of control	≥ 78.9 AND 130% of control
(mid-depth)	station's turbidity on the	station's turbidity on the
	same day of measurement	same day of measurement
рH	pH ≤7.55 or pH ≥ 8.11	pH ≤ 6 or pH ≥ 9

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

Fugro Development Centre, Tel : +852-2450 8233 5 Lok Yi Street, Tai Lam, Fax : +852-2450 6138 Tuen Mun, N.T., E-mail : matlab@fugro.com.hk Hong Kong. Website : www.materialab.com.hk



Ref No.: 100440EN121502

Table 3.2 (Con't)

Parameters	Action Level	Limit Level
Cadmium in µg/L	≥ 0.5	≥ 0.5
Chromium in µg/L	≥ 1	≥ 1
Aluminium in µg/L	≥ 20	≥ 20

Notes:

- 1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
- 2. For SS and turbidity, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

Landfill Gas Limit

Depending on the results of the measurements, actions required will be vary and should be set down by the Safety Officer or other appropriately qualified person. The actions shown in Table 3.3 should be referred as the minimum requirements to be encompassed.

Table 3.3 Action Level for Landfill Gas Measurement

Parameter	Measurement	Action
Oxygen	<19 %	 Ventilate to restore oxygen to >19 %
	<18 %	Stop works
		Evacuate personnel / prohibit entry
		Increase ventilation to restore oxygen to >19 %
Methane	>10 % LEL	Prohibit hot works
	(i.e. >0.5 % by volume)	 Ventilate to restore methane to <10 % LEL
	>20 % LEL	Stop works
	(i.e. >1 % by volume)	Evacuate personnel / prohibit entry
		 Increase ventilation to restore methane to <10 % LEL
Carbon dioxide	>0.5 %	 Ventilate to restore carbon dioxide to <0.5 %
	>1.5 %	Stop works
		Evacuate personnel / prohibit entry
		 Increase ventilation to restore carbon dioxide to <0.5 %

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel: +852-2450 8233
: +852-2450 6138
: matlab@fugro.com.hk
: www.materialab.com.hk



Ref No.: 100440EN121502

4. Construction Phase Environmental Monitoring and Audit

4.1 Review of the construction phase environmental monitoring

4.1.1 Impact water quality monitoring was performed at three locations with two control stations at Tsang Kok Stream; and two marine locations with one control station in Deep Bay Zone. Piling work was commenced on 21 February 2011 and the foundation piling work was completed on 13 October 2011. The pre-bore piling of the STF was completed on 22 February 2012 and the post monitoring for marine water has been completed on 20 March 2012. Although marine water quality monitoring resumed on 03 July 2012 due to the commencement of pre-bore operation for sheet piling, the pre-bore operation as planned was not carry out. Therefore the impact marine water quality monitoring was suspended on 20 August 2012 and post impact monitoring is not required.

Pursuant to Clause 5.7.1.1 of the EM&A Manual, impact water quality monitoring shall be carried out during site formation, piling and construction of the access road. As the above mentioned site construction has been completed on 17 August 2012, four weeks post monitoring was commenced by 20 August 2012 and ended on 14 September 2012 inclusively.

Ecology and Visual Impact monitoring were carried out at the East and the Middle Lagoon. The locations of the water monitoring station selected as the nearest water sensitive receivers are shown in Figure 4.1 and 4.2 of Appendix 7.

Table 4.1 Summary of Environmental Monitoring from 25 August 2012 to 24 November 2012

Monitored	Parameters	25 Aug 2012 to 24 Sept 2012	25 Sept 2012 to 24 Oct 2012	25 Oct 2012 to 24 Nov 2012
Stream water	DO, DOS, pH, SS, Temp and Turbidity	9	Not Required	Not Required
Marine water	Cd, Cr and Al	Not Required	Not Required	Not Required
	Avifauna	1	1	1
Ecology	Habitat	2	2	2
	Vegetation	2	2	2
Landscape	Compliance of mitigation measures	2	2	2

4.1.2 Excavation works has been carried out within the WENT landfill consultation zone for the following construction activities during the reporting period: (1) Portion 1 (next to Plant B, foundations works for east marshalling area); (2) Portion 1 (AEE Storage Yard); (3) Portion 3 (next to Canteen, cable ducting) and (4) Portion 3 (next to T758). No gas monitoring on 23 November 2012 due to flooding of the work area.

Fugro Development Centre,

5 Lok Yi Street, Tai Lam,

Tuen Mun, N.T.,

Hong Kong.

Tel: +852-2450 8233

Fax: +852-2450 6138

E-mail: matlab@fugro.com.hk

Website: www.materialab.com.hk



Ref No.: 100440EN121502

Table 4.2 Summary of Landfill Gas Monitoring

Sampling Location	25 Aug 2012 to 24 Sept 2012	25 Sept 2012 to 24 Oct 2012	25 Oct 2012 to 24 Nov 2012			
Portion 1 (next to Plant B)	52	46	52^			
Portion 1 (AEE Storage Yard)	Not Required#	10	52^			
Portion 3 (next to Canteen)	52	46	Not Required*			
Portion 3 (next to T758)	28	Not Required**	Not Required**			

Remark:

No gas monitoring on 23 Nov 2012 due to flooding of the work area.
 Portion 1 (AEE Storage Yard): Excavation on 18 October 2012.

Portion 3 (next to Canteen): No gas monitoring starting from 25 October 2012 as no works are

carried out inside the opened cable trench.

** Portion 3 (next to T758): Backfilled on 11 September 2012.

4.2 Synopsis of work undertaken during this quarter

During this quarter in review, construction activity undertaken by the Contractor is listed in Table 4.3.

Table 4.3 Construction activity undertaken during 25 August 2012 to 24 November 2012

Table 4.5 C	onstruction activity undertaken during 25 August 2012 to 24 November 2012
Month	Construction task item
25 Aug 2012 to	■ Waterproofing;
24 Nov 2012	Steel Works;
	Strut Erection;
	 Substructure Works: Including Reinforcement, Formwork, Concreting;
	Structure Works: Including Reinforcement, Formwork, Concreting;
	 Assembly of Boiler;
	Structural Steel Erection;
	Roof Installation;
	Mechanical Installation;
	Viewing Gallery Construction;
	*Bridge Construction;
	Heavy Lifting;
	Façade Installation;
	Delivery of Heavy Machineries; On Machineries;
	■ E & M Installation;
	Curtain Wall Installation;
	Gondola Operation;
	Inter Decoration;
	Precast Installation; **Road Works:
	rtoda vvolto,
	opade trade metallation,
	Glass and Steel Installation;Pipe Jacking;
	Cable Laying;
	Condenser Installation;
	Lifting Installation; and
	Water Tank Fixture.
	Water rank rixtare.

Remark:

* The Period of Bridge Construction: 25 Aug 2012 to 24 Oct 2012
 ** The Period of Road Works: 25 Aug 2012 to 24 Sept 2012

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

Fugro Development Centre,

5 Lok Yi Street, Tai Lam,

Tuen Mun, N.T.,

Hong Kong.

Tel: +852-2450 8233

1: +852-2450 6138

Tuen Mun, N.T.,

E-mail: matlab@fugro.com.hk

Website: www.materialab.com.hk



Ref No.: 100440EN121502

4.3 Audit summary of non-compliances of the environmental quality performance limits from 25 August 2012 to 24 November 2012.

Water Quality

The summary of non-compliance is shown in Table 4.4.

Table 4.4 Summary of Monitoring Non-Compliance

Monitored		25 Aug 2012 to 24 Sept 2012		25 Sept 2012 to 24 Oct 2012		25 Oct 2012 to 24 Nov 2012	
Parameter		Action	Limit	Action	Limit	Action	Limit
	Turbidity	0	0	Not Re	quired	Not Required	
Ctroom water	Suspended Solid	0	0	Not Required		Not Required	
Stream water	рН	1	0	Not Required		Not Re	quired
	Dissolved Oxygen	0	0	Not Required		Not Re	quired
	Cadmium	Not Required		Not Re	quired	Not Re	quired
Marine water	Chromium	Not Required		Not Required		Not Required	
	Aluminium	Not Re	equired	Not Required		Not Re	quired

Remark: The number of non-compliances is shown

Ecology Monitoring

No non-compliance was recorded in the reporting quarter.

Landscape and Visual Monitoring

No non-compliance was recorded in the reporting quarter.

Landfill Gas Monitoring

Landfill gas monitoring was carried out by a competent person during the excavation, operation in chamber and confined space within the WENT landfill control zone and no non-compliance was recorded in the reporting quarter.

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel: +852-2450 8233
: +852-2450 6138
: matlab@fugro.com.hk
: matlab@fugro.com.hk



Ref No.: 100440EN121502

4.4 Review of the events of non-compliance

Stream Water Quality

Table 4.5 Summary of reasons for the exceedances of stream water quality

Month	The reasons for the exceedances of stream water quality
Sept 2012	Construction works, include waterproofing, steel works, strut erection, substructure works: (including reinforcement, formwork, concreting), structure works: (including reinforcement, formwork, concreting), assembly of boiler, structural steel erection, roof installation, mechanical installation, bridge construction, heavy lifting, façade installation, delivery of heavy machineries, E & M installation, curtain wall installation, gondola operation, inter decoration, precast installation, road works, space truss installation, glass and steel installation, pipe jacking, cable laying, and condenser installation were in progress throughout the reporting period at the North part of the Lagoon and far away from the Tsang Kok Stream. The stream water quality was at the similar level as that before the piling work.
	1 event of exceedance of pH was recorded at mid-flood during September at W3. Since W3 was located at the downstream of C2, so that the exceedance was subject to the influent of the high pH and the natural flow from C2, and not owing to construction activities related.

4.5 Action taken in the event of non-compliance

Stream Water Quality

In this reporting quarter, 1 event of reported exceedance based on the A/L levels stated in Table 3.2 which are not related to the construction activities, hence, ad-hoc monitoring was not performed.

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

Fugro Development Centre, Tel: +852-2450 8233
5 Lok Yi Street, Tai Lam, Fax: +852-2450 6138
Tuen Mun, N.T., E-mail: matlab@fugro.com.hk
Hong Kong. Website: www.materialab.com.hk



Ref No.: 100440EN121502

5. Summary of Complaints, Summons and Successful Prosecutions

No documented correspondence regarding complaints, summons and successful prosecutions in association with the construction activities was received in this reporting quarter.

Table 5.1 Summary of Environmental Complaints and Prosecutions

Complaints Logged		Summons Served		Successful Prosecution	
Sept 2012 to Nov 2012	Cumulative	Sept 2012 to Nov 2012 Cumulative		Sept 2012 to Nov 2012	Cumulative
0	1	0	0	0	0

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel: +852-2450 8233
: +852-2450 6138
: matlab@fugro.com.hk
: www.materialab.com.hk



Ref No.: 100440EN121502

6. Comments and Conclusions for 25 August 2012 to 24 November 2012

Air Quality

There is no nearby sensitive receiver identified by EIA study hence dust monitoring is not required. The site activities performed in the reporting quarter including vegetation removal, top layer PFA compaction and building works, did not cause significant dust impact. However, the Contractor should deploy necessary dust mitigation measures to reduce potential impacts from construction works to a minimum, which include frequent water spraying at dust generation areas.

Noise Level

Same as air quality, no sensitive receiver is close to the construction site. In the past three months, no deterioration of the environmental noise level is noted.

After commencement of piling works (even the foundation piling work and pre-bore piling were completed on 13 October 2011 and 22 February 2012 respectively), Contractor should deploy necessary noise mitigation measures to minimize the influence to the wildlife in the Middle Lagoon. Close monitoring of any impact to the habitat will be in place.

Water Quality

Stream water

During this reporting quarter, non-compliance of pH was recorded according to the A/L levels stated in Table 3.2. The cause was substantially attributable to influent by high pH from upstream. Impact monitoring data indicates the water quality is similar to that of baseline level. The construction activities were located in the North part of the Lagoon and far apart from the Tsang Kok Stream. Hence, the exceedance recorded is not related to the construction activities.

Marine Water

Marine Water Quality Monitoring was not required in the reporting period.

Ecology Monitoring

Contractor has followed the mitigation measures to prevent any disturbance to the wildlife in the Middle Lagoon. After commencement of the piling work on 21 February 2011, no significant impact to the wildlife was observed. However, the impact of the piling work will be monitored closely (even the foundation piling work and pre-bore piling were completed on 13 October 2011 and 22 February 2012 respectively).

Summary of ecology survey is presented in Appendix 3.

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company,

Fugro Development Centre,

5 Lok Yi Street, Tai Lam,

Tuen Mun, N.T.,

Hong Kong.

Tel: +852-2450 8233

Fax: +852-2450 6138

Tuen Mun, N.T.,

E-mail: matlab@fugro.com.hk

Website: www.materialab.com.hk



Ref No.: 100440EN121502

Landscape and Visual Impact Monitoring

In general, the implementation of the proposed measures in construction phase were followed and no non-compliance was observed in the reporting quarter. Summary of observation during the reporting quarter is enclosed in Appendix 4.

Waste Management Status

C&D Waste Backfill and excavation works were conducted during the

reporting period. C&D waste was generated from the current

activities and sent to public fill.

General refuse Paper / cardboard, metal and plastics were collected by

recycling collectors as far as practicable and general refuse

was collected and sent to WENT Landfill.

Chemical waste 940kg solid chemical waste was generated during the

reporting period and collected by licensed contractor.

Wastewater Rain water was treated by the silt removal facilities before

discharged outside the site. Waste was collected by licensed

collector.

Waste flow summary for the previous months is attached in Appendix 5.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

 Telephone
 : +852-2450 8233

 Telefax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.fugro.com



Appendix 1

Environmental Mitigation Implementation Schedule

MateriaLab Division,Tel: +852-2450 8233Fugro Development Centre,Fax: +852-2450 61385 Lok Yi Street, 17 M.S. Castle Peak Road,E-mail: matlab@fugro.com.hkTai Lam, Tuen Mun, N.T., Hong Kong.Website: www.materialab.com.hk



Table 1. Implementation Schedule and Status of Proposed Air Quality Mitigation Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Imple	ementa	tion St	ages*	Relevant Legislation and Guidelines
				Des	C	0	Dec	
S3.8.1	Implementation of the Air Pollution Control (Construction Dust) Regulation and good site practices:	Work site / During the construction period	Contractor					Air Pollution Control (Construction Dust) Regulation
	Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather.				1			
	• Use of frequent watering for particularly dusty construction areas and areas close to ASRs.				√			
	• Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.				√ ,			
	Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs.				√ 			
	• Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.				V			
	• Establishment and use of vehicle wheel and body washing facilities at the exit points of the site.				√			
	 Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods. 				√			



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			ages*	Relevant Legislation and Guidelines
				Des	C	0	Dec	
	• Imposition of speed controls for vehicles on unpaved site roads. Ten kilometers per hour is the recommended limit.				$\sqrt{}$			
	• Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs.				√			
	• Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.				$\sqrt{}$			

[#] All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

- Des Design, C Construction, O Operation, and Dec Decommissioning
- N/A The associated activities are not in progress during the monitoring month, $\sqrt{\ }$ The proposed mitigation measures is implemented

MateriaLab Division,Tel: +852-2450 8233Fugro Development Centre,Fax: +852-2450 61385 Lok Yi Street, 17 M.S. Castle Peak Road,E-mail: matlab@fugro.com.hkTai Lam, Tuen Mun, N.T., Hong Kong.Website: www.materialab.com.hk



Table 2. Implementation Schedule of Proposed Human Health Risk Mitigation Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Imple	mentat	ion Sta	ages*	Relevant Legislation and Guidelines
				Des	С	0	Dec	
	Human Health Risk Associated with Radon							
	 Prevention of radon influx from the PFA to the STF buildings A soil cover can be provided beneath the buildings on top of ash lagoon prior to construction works because it reduces the level of radon influx significantly 	STF buildings / During the design, construction and operation of the STF.	Contractor / STF Operator		N/A			EPD's ProPECC Note PN 1/99 Control of Radon Concentration in New Buildings Appendix 2
	 Slab-on-grade can be an option on foundation design Soil suction can also prevent radon from entering the building by drawing the radon from below the building and venting it through a pipe, or pipes, to the air above the building. 				N/A N/A			
	 Provision of Sufficient ventilation of the interior of the STF buildings Forced and natural ventilation should be introduced properly to enhance air exchange rate in the STF buildings. 				N/A			
	Basement areas should be pressurized by using a fan to blow air into the basement areas from outdoors is suggested. This would create enough pressure at the lowest level indoors to prevent radon from entering into the STF buildings.				N/A			
	Regular maintenance for the floor slabs and walls Cracks and other openings in the foundation should be properly sealed to reduce radon ingress. Sealing the cracks limits the flow of radon into the building thereby making other radon reduction techniques more effective and cost-efficient. It also reduces the loss of conditioned air.				N/A			

- # All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.
- Des Design, C Construction, O Operation, and Dec Decommissioning
- N/A The associated activities are not in progress during the monitoring month, $\sqrt{\ }$ The proposed mitigation measures is implemented. The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Tel :+852-2450 8233
Fugro Development Centre, Fax :+852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materialab.com.hk



Table 3. Implementation Schedule of Proposed Waste Management Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	/ Timing Implementation Agent	Impl	ement	ation S	stages*	Relevant Legislation and Guidelines
				Des	C	0	Dec	
\$5.5.1	Good Site Practices Recommendations for good site practices during the construction activities include:	Work site / During the construction period	Contractor					Waste Disposal Ordinance (Cap.354)
	Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site				√			ETWB TCW No. 19/2005
	Training of site personnel in proper waste management and chemical handling procedures				√			
	Provision of sufficient waste disposal points and regular collection of waste				V			
	Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers				1			
	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.				V			
S5.5.1	Waste Reduction Measures	Work site / During planning & design	Contractor		,			
	• Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:	stage, and construction stage			√			



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Impl	ementa	ntion St	ages*	Relevant Legislation and Guidelines
				Des	C	О	Dec	
	The design of the foundation works should minimize the amount of excavated material to be generated.				√			
	• Excavated soil should be reused on site as far as possible, e.g. for landscape works, in order to minimize the amount of public fill to be disposed off-site.				√			
	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.				V			
	Encourage collection of aluminium cans by individual collectors by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the work force				V			
	• Proper storage and site practices to minimize the potential for damage or contamination of construction materials.				√			
	Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste.				V			
S5.5.1	General Refuse General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.	Work site / During the construction period	Contractor		√			Public Health and Municipal Services Ordinance (Cap. 132)



		Location / Timing	Implementation	Imple	mentat	ion Sta	ges*	Relevant
EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / 1 mining	Agent	Des	C	0	Dec	Legislation and Guidelines
S5.5.1	Construction and Demolition Material							
	In order to minimize the impact resulting from collection and transportation of C&D material for off-site disposal, the excavated material arising from site formation and foundation works should be reused on-site as backfilling material and for landscaping works as far as practicable. Other mitigation requirements are listed below:	Work site / During design stage & construction period	Contractor	√	√			ETWB TCW No. 33/2002 ETWB TCW No. 19/2005 ETWB TCW No. 31/2004
	A Waste Management Plan, which becomes part of the Environmental Management Plan, should be prepared in accordance with ETWB TCW No.19/2005.				√			
	A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be proposed.				√			
	• In order to monitor the disposal of C&D material at public filling facilities and landfills and to control fly-tipping, a trip-ticket system should be included. One may make reference to ETWB TCW No. 31/2004 for details.				√			
S5.5.1	Chemical Waste							
	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible	Work site / During the construction period	Contractor		√			Waste Disposal (Chemical Waste)(General) Regulation)

MateriaLab Division, Tel :+852-2450 8233
Fugro Development Centre, Fax :+852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materialab.com.hk



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Location / Timing	Implementation Agent	Impler	nentat	ion Sta	iges*	Relevant Legislation and
			8	Des	C	0	Dec	Guidelines	
	chemicals should be stored separately. Appropriate labels should								
	be securely attached on each chemical waste container indicating								
	the corresponding chemical characteristics of the chemical waste,								
	such as explosive, flammable, oxidizing, irritant, toxic, harmful,								
	corrosive, etc. The Contractor shall use a licensed collector to								
	transport and dispose of the chemical wastes, to either the								
	Chemical Waste Treatment Centre at Tsing Yi, or another								
	licensed facility, in accordance with the Waste Disposal								
	(Chemical Waste) (General) Regulation.								

All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

- Des Design, C Construction, O Operation, and Dec Decommissioning
- N/A The associated activities are not in progress during the monitoring month, $\sqrt{\ }$ The proposed mitigation measures is implemented

MateriaLab Division,Tel: +852-2450 8233Fugro Development Centre,Fax: +852-2450 61385 Lok Yi Street, 17 M.S. Castle Peak Road,E-mail: matlab@fugro.com.hkTai Lam, Tuen Mun, N.T., Hong Kong.Website: www.materialab.com.hk



Table 4. Implementation Schedule of Proposed Land Contamination Preventive Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Imple	mentat	ion Sta	ıges*	Relevant Legislation and Guidelines
				Des	C	0	Dec	
S5.6.3	 Fuel Oil Tank Construction and Test The fuel tank to be installed should be of specified durability Double skin tanks are preferable Underground fuel storage tank to be installed should be placed within a concrete pit The concrete pit shall be accessible to allow regular tank integrity tests to be carried out at regular intervals The tank integrity tests should be conducted by an independent qualified surveyor or structural engineer Any potential problems identified in the test should be 	Fuel Oil Storage Tank /	Contractor/ STF Operator	√ V	√			
S5.6.3	rectified as soon as possible Fuel Oil Pipeline Construction and Test Installation of aboveground fuel oil pipelines is preferable; if underground pipelines are unavoidable, concrete lined trenches should be constructed to contain the pipelines Double skin pipelines are preferable Distance between the fuel oil refuelling points and the fuel oil storage tank shall be minimized The integrity tests for the pipelines should be conducted by an independent qualified surveyor or structural engineer at regular intervals Any potential problems identified in the test should be rectified as soon as possible	Fuel Oil Pipelines/ Design, Construction and Operation Phase	Contractor/ STF Operator	V	\ \ \ \			
S5.6.3	Fuel Oil Leakage Detection Installation of leak detection device at storage tank and pipelines	Fuel Oil Storage Tank	Contractor/ STF Operator	N/A	N/A			

[#] All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project.

Page 8 of 20

[•] Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

[•] N/A – The associated activities are not in progress during the monitoring month, $\sqrt{\ }$ - The proposed mitigation measures is implemented

MateriaLab Division, Tel :+852-2450 8233
Fugro Development Centre, Fax :+852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materialab.com.hk



Table 5. Implementation Schedule of Proposed Water Pollution Control Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Imple	mentat	ion Sta	Relevant Legislation and Guidelines	
				Des	C	О	Dec	und Guidennes
S6.7.2	 Construction Runoff and Drainage Site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" shall be followed as far as practicable in order to minimize surface runoff and the chance of erosion: At the start of site establishment, internal drainage works and erosion and sedimentation control facilities shall be implemented. Channels, earth bunds or sand bag barriers shall be provided on site to direct stormwater to silt removal facilities. The detailed design and installation of the temporary on-site drainage system shall be undertaken by the contractor prior to the commencement of construction. Before commencing any site formation work, all sewer and drainage connections shall be sealed to prevent debris, soil, sand etc. from entering public sewers/drains. Boundaries of earthworks shall be surrounded by dykes or embankments for flood protection, as necessary. 	Work site / During the construction period	Contractor	Des	C √ N/A	0	Dec	ProPECC PN 1/94; WPCO
	• Sand/silt removal facilities such as sand traps, silt traps and sediment basins shall be provided to remove				V			
	sand/silt particles from runoff to meet the standards of the Technical							



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			Relevant Legislation and Guidelines	
				Des	C	0	Dec	
	Memorandum under the Water Pollution Control							
	Ordinance. The design of silt removal facilities shall							
	be based on the guidelines provided in ProPECC PN							
	1/94. All drainage facilities and erosion and sediment							
	control structures shall be inspected monthly and							
	maintained to ensure proper and efficient operation at							
	all times and particularly during rainstorms.							
	• Water pumped out from foundation piles shall be				N/A			
	discharged into silt removal facilities.				,			
	• During rainstorms, exposed slope/soil surfaces shall				√			
	be covered by a tarpaulin or other means, as far as							
	practicable. Other measures that need to be							
	implemented before, during and after rainstorms are							
	summarized in ProPECC PN 1/94.							
	Exposed soil areas shall be minimized to reduce				V			
	potential for increased siltation and contamination of							
	runoff.							
	• Earthwork final surfaces shall be well compacted and				V			
	subsequent permanent work or surface protection							
	shall be immediately performed. Open stockpiles of							
	construction materials or construction wastes on- site							
	of more than 50m3 shall be covered with tarpaulin or							
	similar fabric during rainstorms.							
	All vehicles shall be cleaned before leaving the works				'			
	area to ensure no earth, mud and debris is deposited							
	on roads. An adequately designed and							



	Environmental Protection Measures / Mitigation	I andian / Timina	II	Imple	mentat	ion Sta	iges*	Dalamant I anialation
EIA Ref#	Measures	Location / Timing	Implementation Agent	Des	C	О	Dec	Relevant Legislation and Guidelines
	sited wheel washing bay shall be provided at every site exit. The wheel washing facility shall be designed to minimize the intake of surface water (rainwater). Wash-water shall have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process.							
S6.7.2	 Debris and refuse generated on-site shall be collected, handled and disposed of properly to avoid entering the nearby water bodies and public drainage system. Stockpiles of cement and other construction materials shall be kept covered when not being used. Oils and fuels shall only be used and stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to nearby water bodies and public drains, all fuel tanks and storage areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund shall be drained of rainwater after a rain event. 	Work site / During the construction period	Contractor		√ √			ProPECC PN 1/94;
S6.7.2	Temporary sanitary facilities, such as portable chemical toilets, shall be employed on-site where necessary to handle sewage from the workforce. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities.	Work site / During the construction period	Contractor		√			ProPECC PN 1/94; WPCO



	Environmental Protection Measures / Mitigation	Location / Timing	Implementation Agent	Imple	mentati	ion Sta	ges*	Delevent Logislation
EIA Ref#	Measures	Location / Timing	Implementation Agent	Des	С	0	Dec	Relevant Legislation and Guidelines
S6.7.2	Release of PFA Leachate from Ash Lagoon into the Aquatic Environment	Deep Bay	Contractor					WPCO
	• Environmental monitoring and audit (EM&A) should be included to ensure that the foundation construction would not cause an unacceptable release of PFA leachate into the Deep Bay waters. The parameters to be measured should include the heavy metals such as cadmium, chromium and aluminium, which have the greatest tendency to leach from the lagooned PFA into the seawater. Details of the measurement requirements are presented in the EM&A manual				V			

- All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and/or accepted public comment to the proposed project.
- Des Design, C Construction, O Operation, and Dec Decommissioning
- N/A The associated activities are not in progress during the monitoring month, $\sqrt{\ }$ The proposed mitigation measures is implemented

MateriaLab Division, Tel :+852-2450 8233
Fugro Development Centre, Fax :+852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materialab.com.hk



Table 6. Implementation Schedule of Proposed Ecological Mitigation Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			Relevant Legislation and Guidelines	
				Des	C	0	Dec	
S7.8.2	Measures to Minimize Disturbance Impact to Wildlife							
	 Hoarding of 3m high shall be set up along the boundary of the works areas and associated site access to shield the fauna and breeding population of Little Grebe in the Middle Lagoon from the disturbance impact of machinery. 	Phase	Contractor		√			
	• The works boundaries shall not go beyond the proposed Project Area. All work crews, equipment and human activities shall be confined within the designated works area only. No personnel should encroach or wilfully disturb any wild animals and their habitats. Traffic and human access from the		Contractor		V			
	 western side of the Project Area should be avoided. Fencing with climbers or plantation shall be provided, where appropriate, along the STF site boundary and the two sides of access road to screen the surrounding habitats from the STF works areas. 	Boundary of works areas/ Operation Phase	Contractor		√			



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	С	0	Dec	
S7.8.2	Measures to Minimize Impact to natural habitats							
	Where practicable, all proposed works shall be conducted in existing built up area to minimize impact to natural habitats.	Works areas/ Design and Construction Phase	STF Designer/ Contractor	√	V			
	• The abutment (permanent structure) for the vehicular bridge shall avoid streambed. The number and size of the temporary supporting structures to be installed over the streambed during construction shall be minimized as far as practicable.	Vehicular bridge/ Design and Construction Phase	STF Designer/ Contractor	√	√			ETWB TC (Works)
	 The temporarily affected natural habitats, including streambed, shall be reinstated after the completion of works. For affected natural stream section, placement of substrates of similar size and composition to those of original streambed shall be considered to encourage colonization. 	Works Area/ Operation Phase Works Area/ Operation Phase	Contractor		N/A			No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works
S7.8.2	 Minimise sedimentation/water quality impacts to waterbodies Measures to control potential sedimentation/ water quality impacts during the construction phase shall be implemented. To minimize the potential water quality impacts from the construction works located at any river channels, natural streams or seafront, the practices outlined in 	Whole Site/ Construction Phase	Contractor		√ √			ETWB TC (Works) No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			Relevant Legislation and Guidelines	
				Des	C	0	Dec	
	ETWB TC (Works) No. 5/2005 "Protection of natural streams/rivers from adverse impacts arising from construction works" shall be adopted where applicable.							
S7.8.2	 Minimize noise disturbance Noise mitigation measures including the use of quieter piling machinery and construction plants shall be implemented to lower the noise level due to construction works. Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction programme. Machines and plant which may be in intermittent use shall be shut down to a minimum. Plant known to emit noise strongly in one direction, shall be oriented so that the noise is directed away from the Middle Lagoon, where possible. Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction period. Mobile plant (such as generator) shall be sited as far away from the Middle Lagoon as possible. Material stockpiles and other structures shall be effectively utilized, where practicable, to screen noise from on-site construction activities. 	Whole Site/ Construction Phase	Contractor		√			ETWB TC (Works) No. 5/2005 Protection of natural streams/ rivers from adverse impacts arising from construction works

MateriaLab Division, Tel :+852-2450 8233
Fugro Development Centre, Fax :+852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materialab.com.hk



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			Relevant Legislation and Guidelines	
				Des	С	0	Dec	
S7.8.3	Measures to Mitigate the Loss of Vegetation	Whole Site / Design,	Contractor / STF					
	• All vegetation located within the work areas shall be	Construction and	Operator					
	preserved as far as practicable.	Operation Phase			$\sqrt{}$			
	• To compensate for the loss of the vegetation and							
	habitats, tree planting shall be provided in the site area							
	where possible. Species chosen for planting shall be							
	similar to the species identified in the survey and be							
	native to Hong Kong or the Southern China.							
S7.8.4	Enhancement Measures to Create Additional Habitat for	Within Project Area/	Contractor / STF					
	Little Grebe	Design Phase,	Operator					
	• An additional habitat for Little Grebe shall be created	Construction and			N/A			
	in a less disturbed area located at the northeastern part of the proposed STF.	Operation Phase						
	• The created habitat shall be provided in form of				N/A			
	shallow pond(s) incorporating suitable habitat				14/11			
	characteristics for Little Grebe. The water level of the							
	created pond shall be kept between 1.5 m to 2 m.							
	Emergent vegetation shall be planted and fish				N/A			
	population shall be controlled to allow development							
	of aquatic invertebrate populations as prey of Little							
	Grebe.							
	To screen the created habitat from disturbance due to				N/A			
	nearby landfill traffic, planting of native plants shall							
	be provided on the boundary of the pond(s) as							
	appropriate.							
	• Prior to construction of the pond(s), detailed Habitat				N/A			
	Creation and Management Plan (HCMP) of the							
	created habitat prepared by experienced ecologist(s)							
	with over seven year experience in relevant field shall							
	be circulated to relevant departments including AFCD							
	for comment.							

- # All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.
- Des Design, C Construction, O Operation and Dec Decommissioning
- N/A The associated activities are not in progress during the monitoring month, $\sqrt{\ }$ The proposed mitigation measures is implemented

Page 16 of 20

MateriaLab Division, Tel :+852-2450 8233
Fugro Development Centre, Fax :+852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materialab.com.hk



Table 7. Implementation Schedule for Landscape and Visual Impact

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			ıges*	Relevant Legislation and Guidelines
				Des	C	О	Dec	
T able 9.4 CM-01	<u>Contaminant/ Sediment Control</u> — Suitable temporary barriers, covers and drainage provisions shall be provided around construction works to avoid discharge of contaminants (such as bleeding from in-situ concrete works) and sediments into sensitive water-based habitats, especially the tidal streams and the mangrove.	Work site / During the construction period	Contractor		V			
T able 9.4 CM-02	Early Planting of Tall Trees – Tall trees proposed under mitigation measure OM-02 shall be planted early, providing visual effect also during construction.	Work site / During the construction period	Contractor		N/A			
T able 9.4 CM-03	Good Site Practice – Construction activities should be restricted to works areas and should be clearly demarcated onsite. Piling of construction materials onsite shall be carefully considered for possible impacts before carrying out.	Work site / During the construction period	Contractor		V			
T able 9.4 CM-04	Existing Trees within Works Areas – All existing trees within work sites shall be properly maintained and protected for their crowns, trunks and roots.	Work site / During the construction period	Contractor	V	1			
T able 9.4 OM-01	Sensitive Bridge Design – The bridge of the proposed access road shall be sensitively designed to minimize impact to the tidal stream and mangrove. It shall be constructed with minimal use of in-situ concreting and with maximum use of precast or prefabricated elements. No pile or support shall be erected within the stream channel.	Bridge of access road / During the design & construction phases	Contractor	V	N/A			



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	С	0	Dec	
T able 9.4 OM-02	Tall trees for Chimney – Fast-growing tall trees shall be planted along the east side of the ash-lagoon to counterbalance possible exotic silhouettes, such as from the chimney, of the proposed sludge treatment facilities for sensitive viewers in Pak Nai. The trees shall be planted during the early stage of the construction to ensure effectiveness during operation. They will also help to lessen the visual impact during construction, as already suggested in mitigation measure CM-02.	East side of ash lagoon / During the design & construction phases	Contractor	1	N/A			
Table 9.4 OM-03	Suitable Reinstatement at Ash-lagoon – Affected perimeter of the proposed works area within the ash-lagoon shall be reinstated with suitable planting materials. Traditional reinstatement planting approach for construction projects may not work well for this project. Certain existing grasses and small shrubs have self-seeded the ash-lagoon, demonstrating their tolerance to salts, alkalinity and possible trace metals in the ash. Therefore the same or similar species of vegetation shall be used.	Perimeter of works area / During the design & construction phases	Contractor	V	N/A			
Table 9.4 OM-04	Existing Tree Transplanting – The proposed access roadworks may affect few existing trees, which shall be transplanted as far as practical. A comprehensive tree survey is recommended to locate these trees.	Access road / During the design & operation phases	Contractor	1	N/A			
Table 9.4 OM-05	<u>Planting at Road Intersection</u> – Suitable planting of woodland trees and shrubs shall be provided for the proposed access roadworks at the junction with Nim Wan Road.	Junction of access road with Nim Wan Road / During the design & operation phases	Contractor	V	N/A			

[#] All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

[•] Des - Design, C - Construction, O - Operation and Dec – Decommissioning

[•] N/A – The associated activities are not in progress during the monitoring month, $\sqrt{\ }$ - The proposed mitigation measures is implemented

MateriaLab Division, Tel :+852-2450 8233
Fugro Development Centre, Fax :+852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materialab.com.hk



Table 8. Implementation Schedule of Proposed Landfill Gas Hazard Protection Measures

EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			Relevant Legislation and Guidelines	
				Des	C	0	Dec	
S10.7.2	Appointment of Safety Officer Appoint a properly trained safety officer and provide with appropriate equipment to measure and monitor LFG hazard.		Contractor		V			
S10.7.2	Safety Measures - Excavation Staff should receive appropriate training on working in areas susceptible to landfill gas, fire and explosion hazards. Excavation procedures and code of practice should be implemented.	Work Site / During the construction phase	Contractor		√			
S10.7.2	Safety Measures – Welding, Flame-Cutting and Hot works Hot works should be confined to open areas away from any trench or excavation. Should hot works must be carried out in trenches or confined space, "permit to work" procedures should be followed.	Work Site / During the construction phase	Contractor		V			
S10.7.2	Safety Measures – Enclosed Spaces Site offices or buildings located within WENT Landfill Consultation Zone which have the capacity to accumulate landfill gas, then they should either be located in an area which has been proven to be free of landfill gas; or be raised clear of the ground by a minimum of 500mm.	Enclosed Spaces within WENT Consultant Zone / During the construction phase	Contractor		N/A			
S10.7.2	Safety Measures – Electrical Equipment Any electrical equipment, such as motors and extension cords, should be intrinsically safe.	Work Site / During the construction phase	Contractor		N/A			

MateriaLab Division, Tel :+852-2450 8233
Fugro Development Centre, Fax :+852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road, E-mail : matlab@fugro.com.hk
Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materialab.com.hk



EIA Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*			Relevant Legislation and Guidelines	
				Des	C	О	Dec	
S10.7.2	Safety Measures – Piping During piping assembly or conduiting construction, all valves/seals should be closed immediately after installation. As construction progresses, all valves/seals should be closed as installed to prevent the migration of gases through the pipeline/conduit. All piping/conduiting should be capped at the end of each working day.	Work Site / During the construction phase	Contractor		N/A			
S10.7.2	Safety Measures – Fire Safety Adequate fire safety equipments should be provided on site. Workers and visitors should be notified of the potential fire hazards. Safety notices should be posted around the site warning the anger and potential hazards.	Work Site / During the construction phase	Contractor		V			
S10.7.2	Safety Measures – Confined Spaces Precautionary measures should include ensuring that staff members are aware of the potential hazards of working in confined spaces, and that appropriate monitoring procedures are in place to prevent hazards in confined spaces.	Confined Spaces at Work Site / During the construction phase	Contractor		N/A			
S10.7.2	Monitoring Periodically during ground-works within the Consultation Zone, the works area should be monitored for methane, carbon dioxide and oxygen using appropriately calibrated portable gas detection equipment. The monitoring frequency and areas to be monitored shall be set down prior to commencement of ground-works. Depending on the results of the measurements, actions required will vary. As a minimum these should encompass those actions specified in Table 10.6 of the EIA Report.	Work Site / During the construction phase	Contractor		N/A			

- All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.
- Des Design, C Construction, O Operation and Dec Decommissioning
- N/A The associated activities are not in progress during the monitoring month, $\sqrt{\ }$ The proposed mitigation measures is implemented

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




Appendix 2

Graphical Presentation of Water Quality Monitoring Data

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W1 - Dissolved Oxygen Content

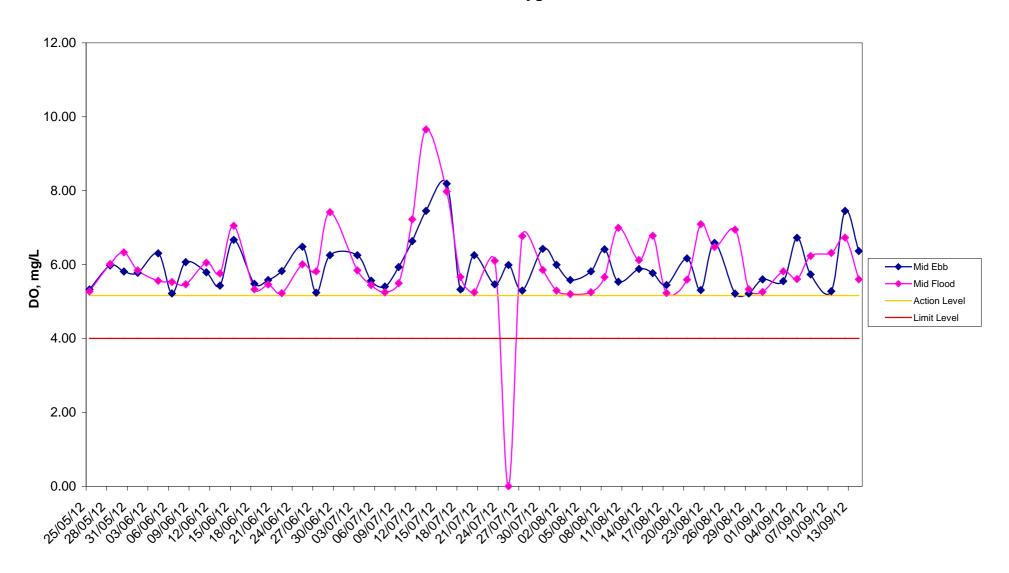

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W1 - Turbidity (Mid-Ebb)

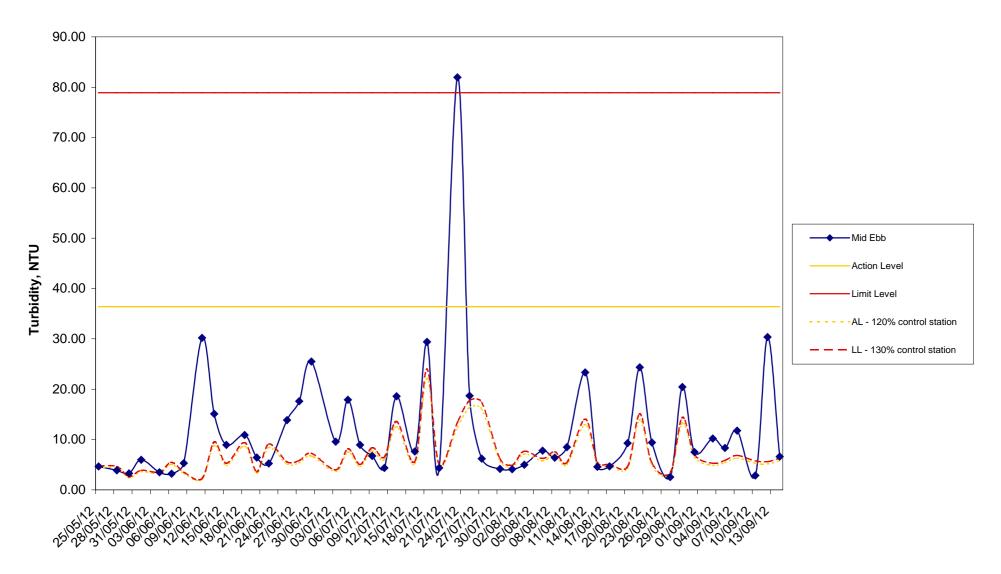

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W1 - Turbidity (Mid-Flood)

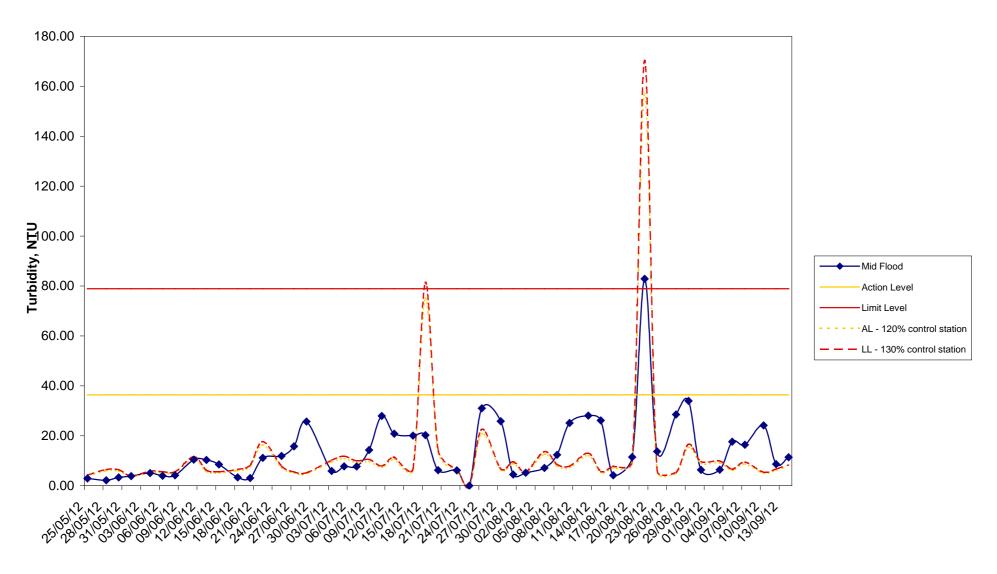

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W1 - pH

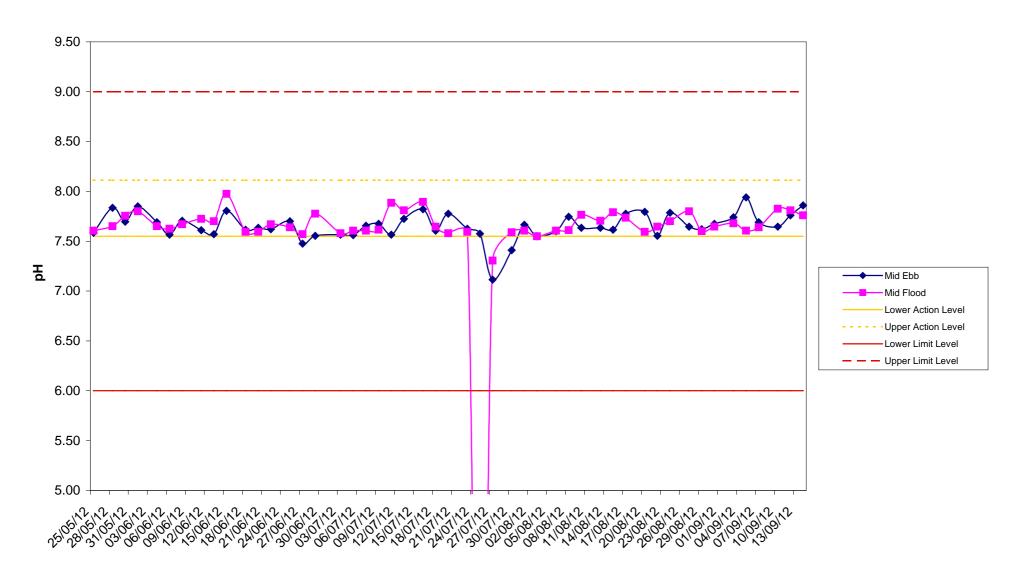

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W1 - Suspended Solid Content (Mid-Ebb)

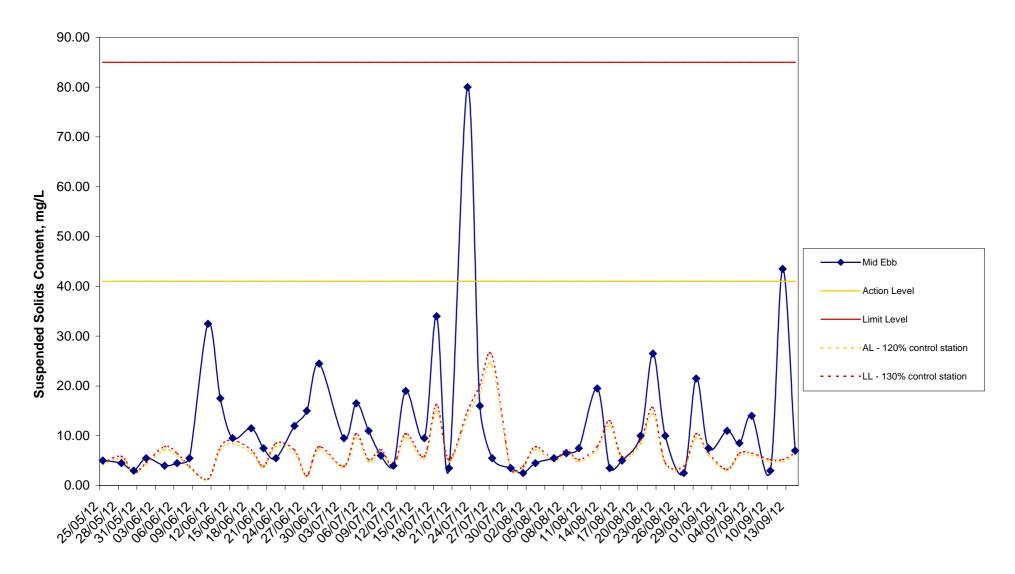

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W1 - Suspended Solids Content (Mid-Flood)

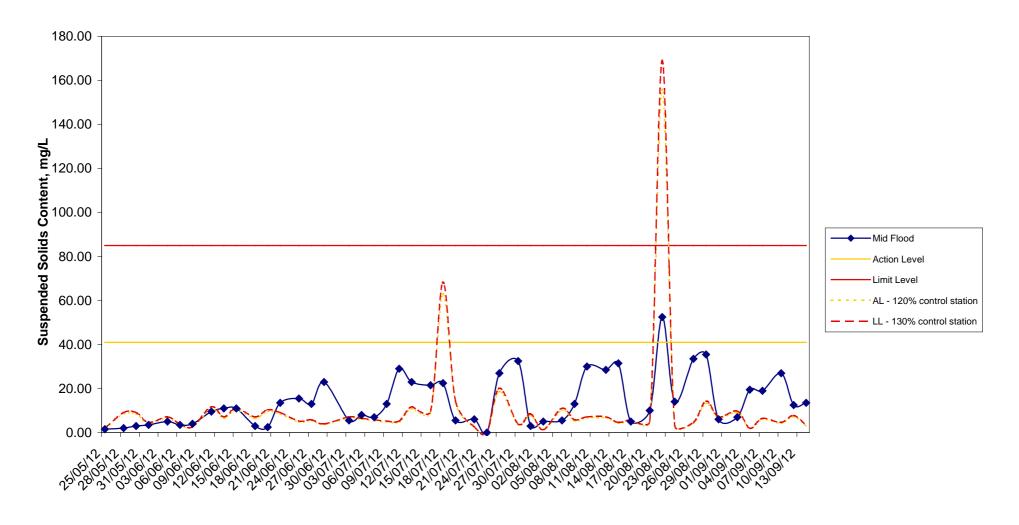

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W2 - Dissolved Oxygen Content

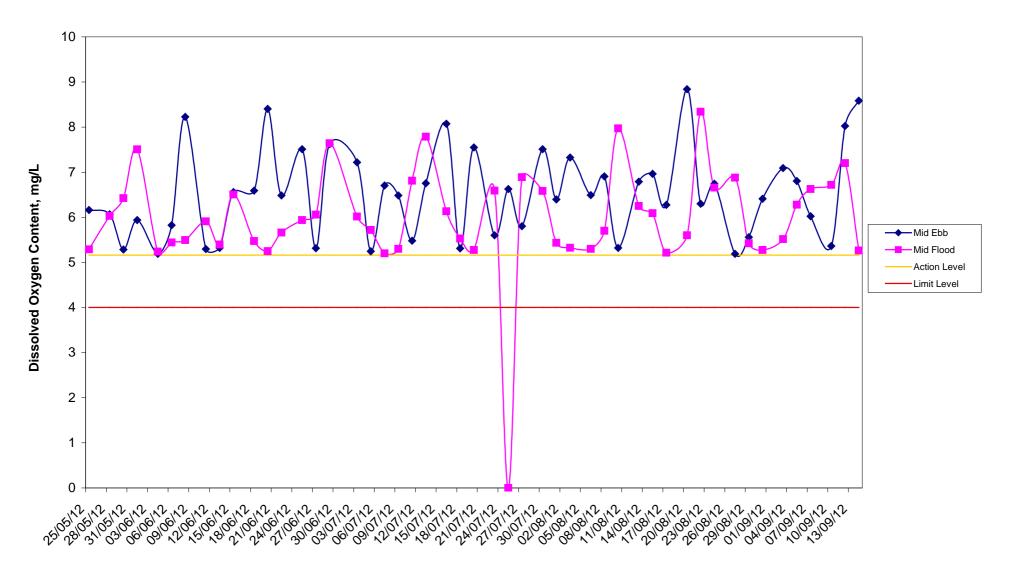

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W2 - Turbidity (Mid-Ebb)

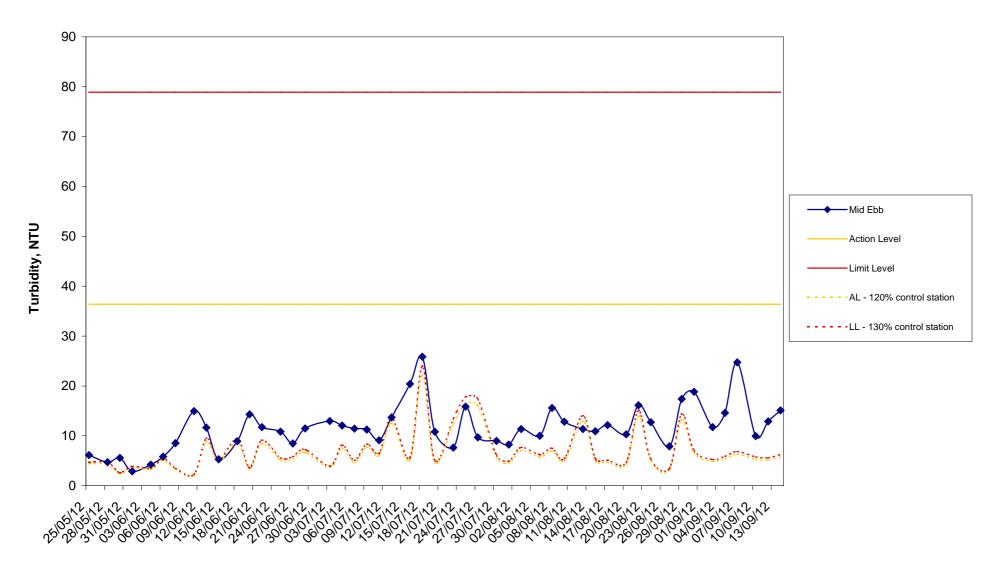

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W2 - Turbidity (Mid-Flood)

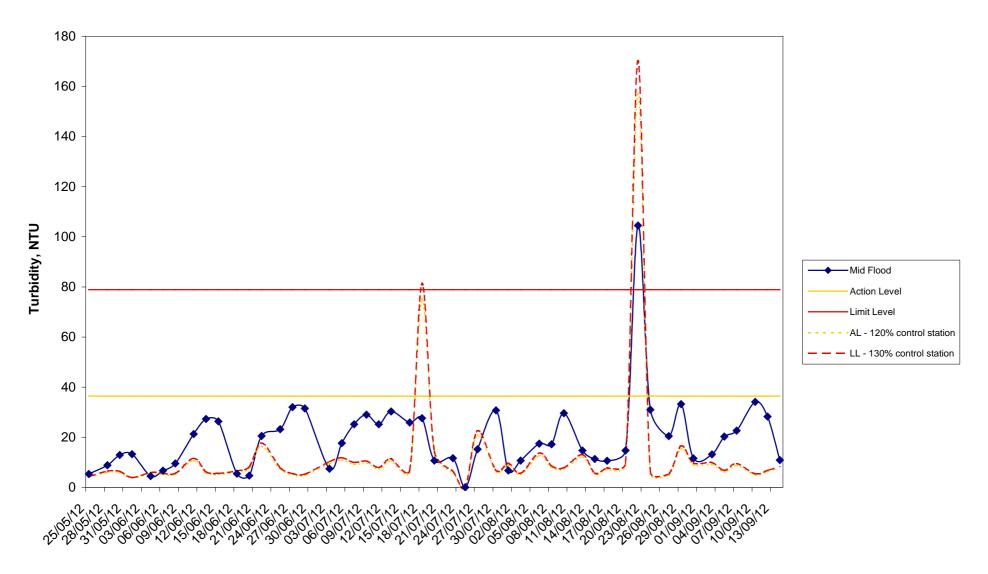

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W2 - pH

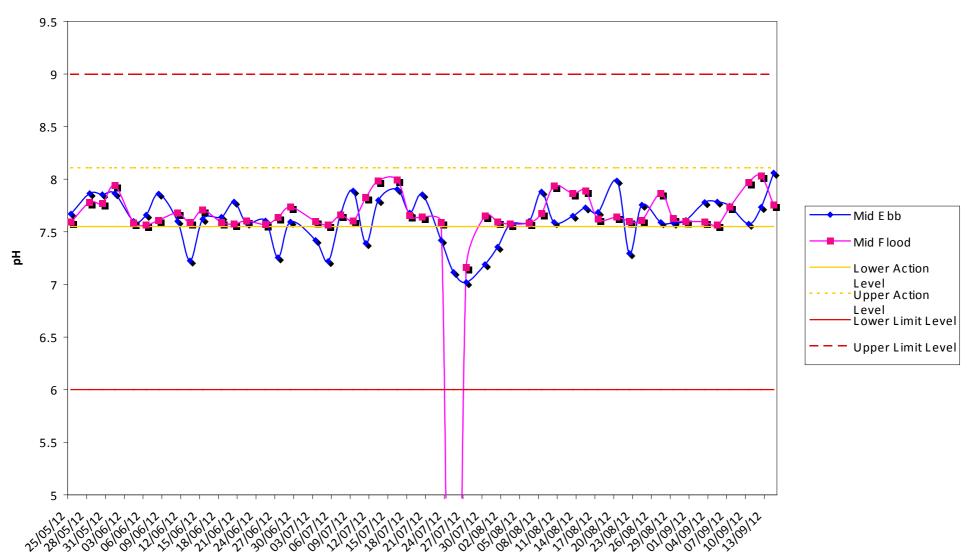

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W2 - Suspended Solids Content (Mid-Ebb)

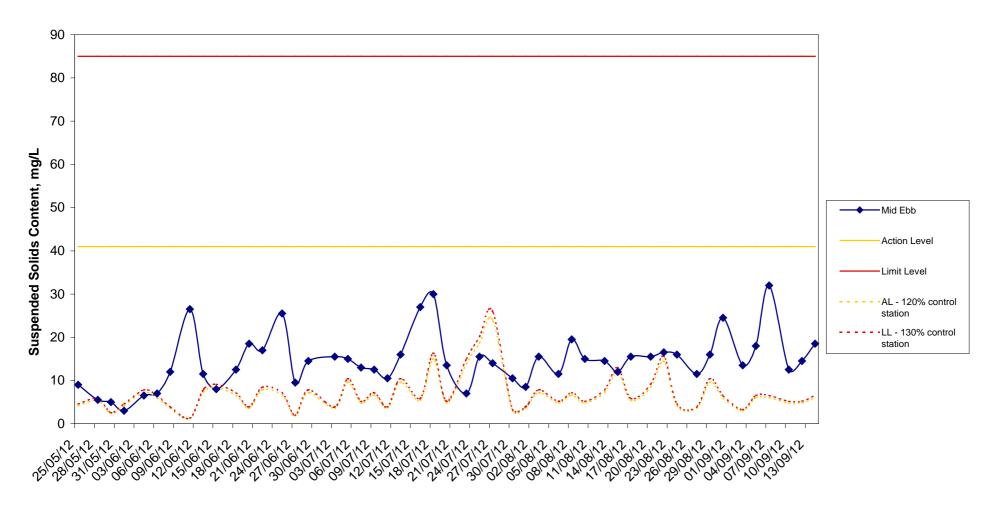

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W2 - Suspended Solids Content (Mid-Flood)

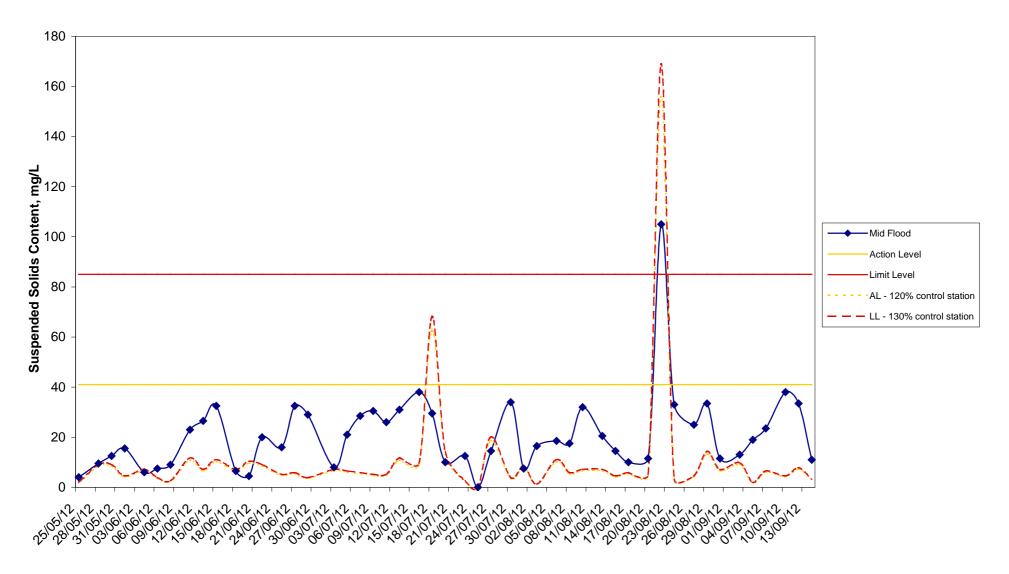

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W3 - Dissolved Oxygen Content

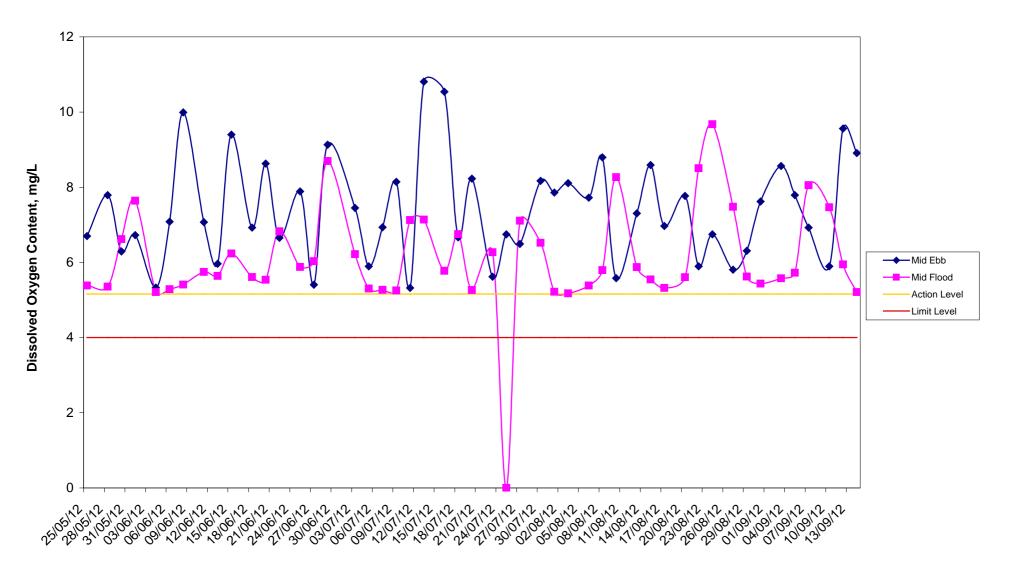

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W3 - Turbidity (Mid-Ebb)

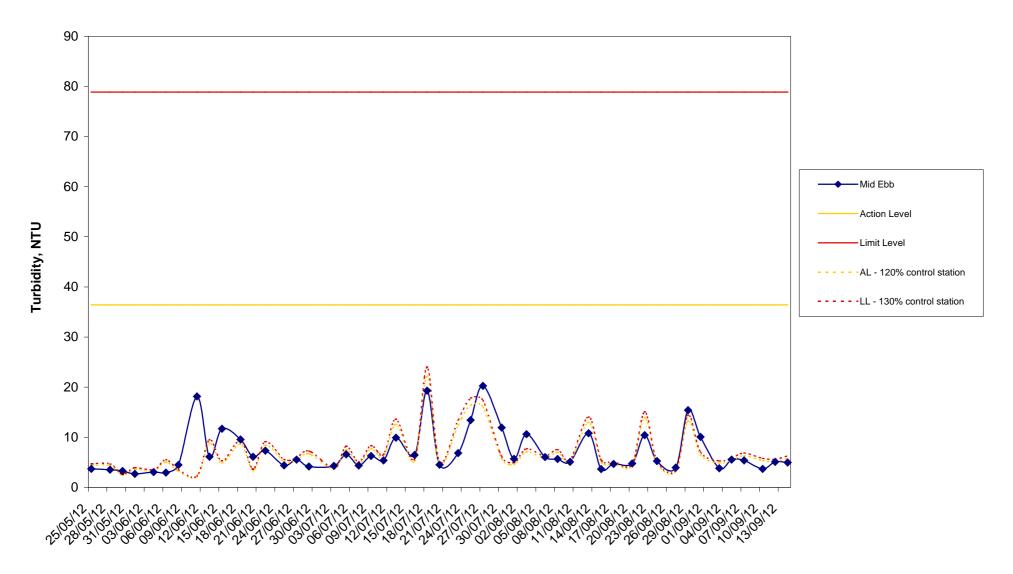

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W3 - Turbidity (Mid-Flood)

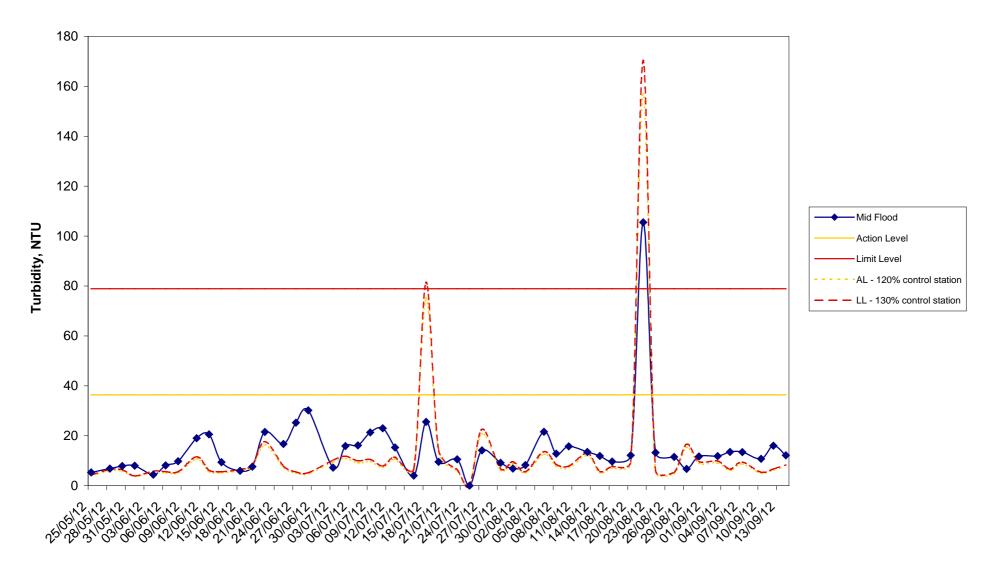

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W3 - pH

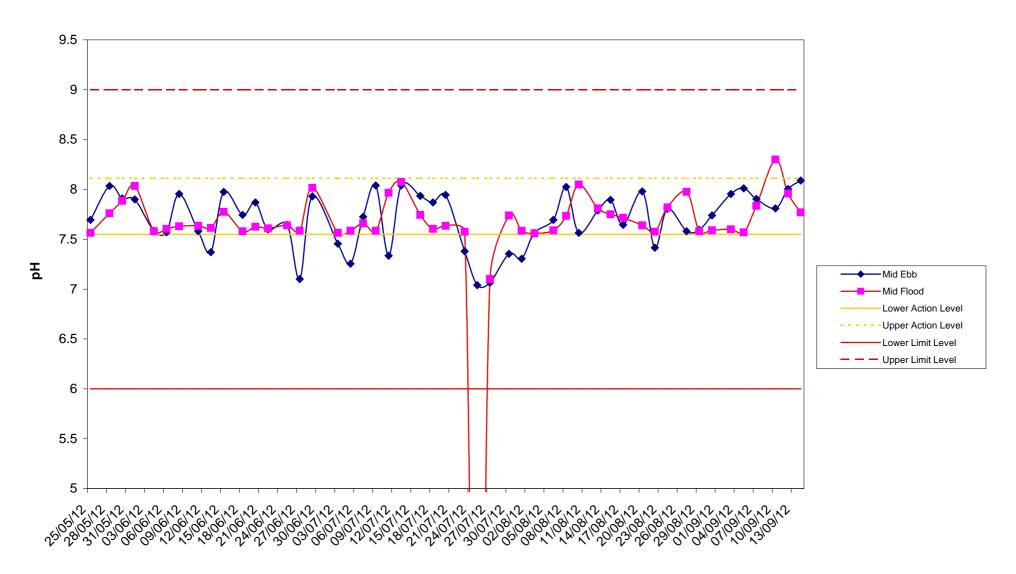

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W3 - Suspended Solids Content (Mid-Ebb)

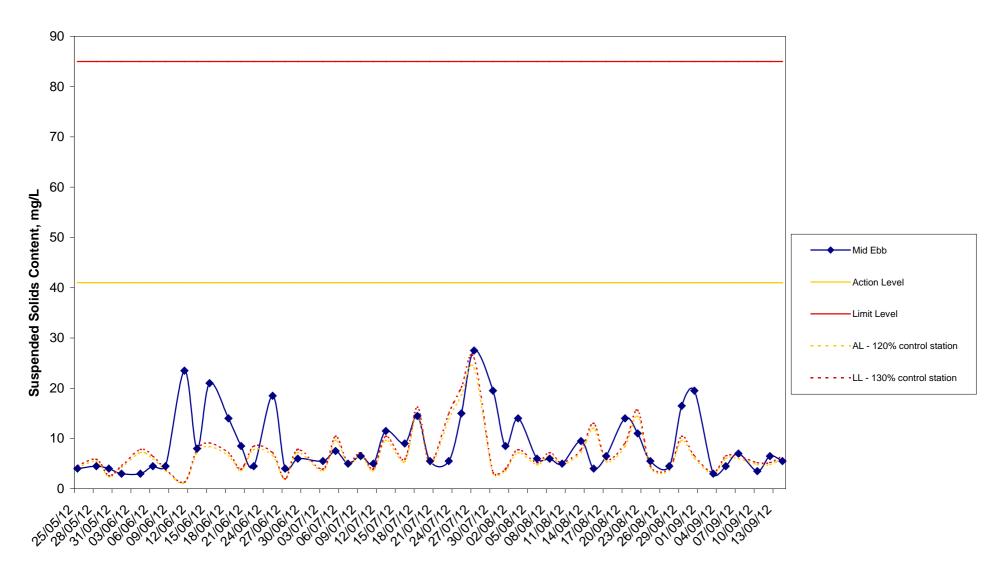

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




W3 - Suspended Solids Content (Mid-Flood)

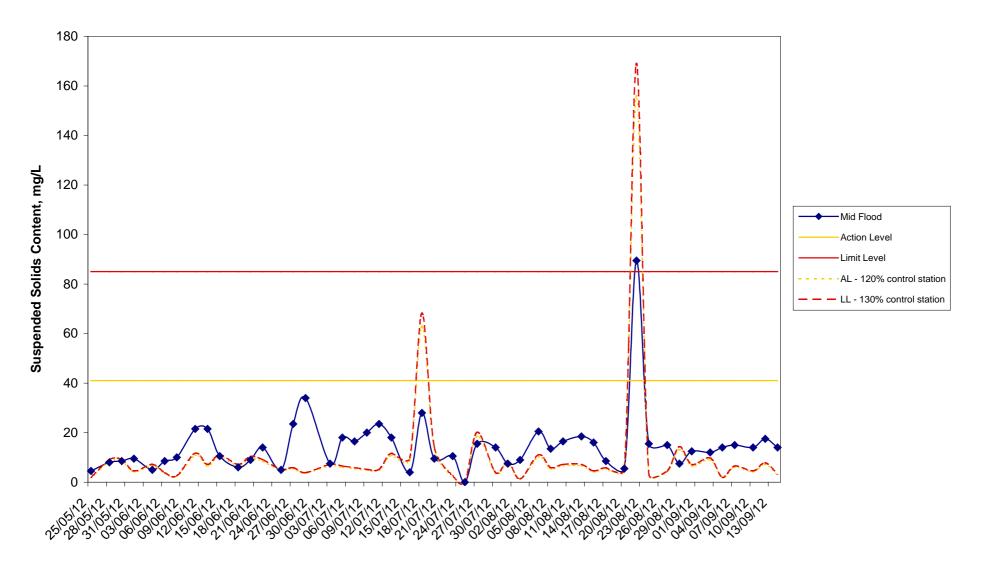

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C1 - Dissolved Oxygen Content

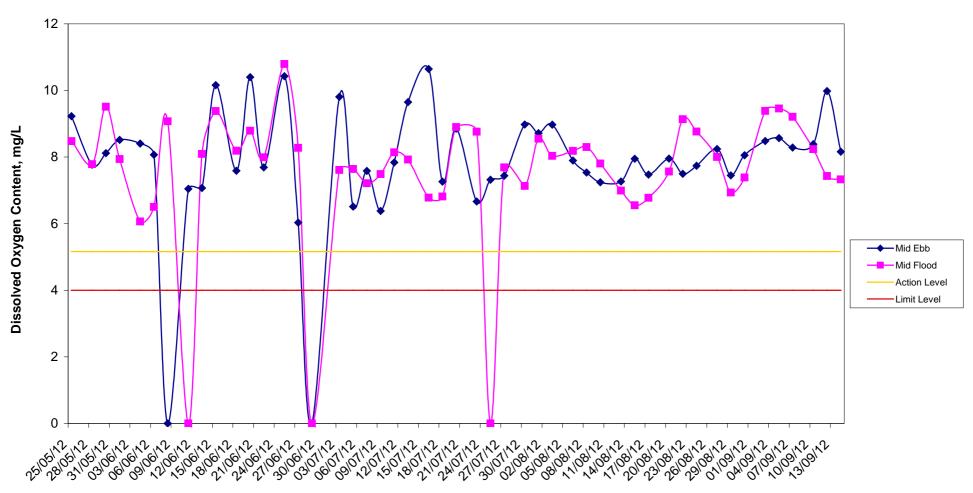


Remark: No water at C1 occasionally after 17/02/2011. Zero values are shown in the graph

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C1 - Turbidity

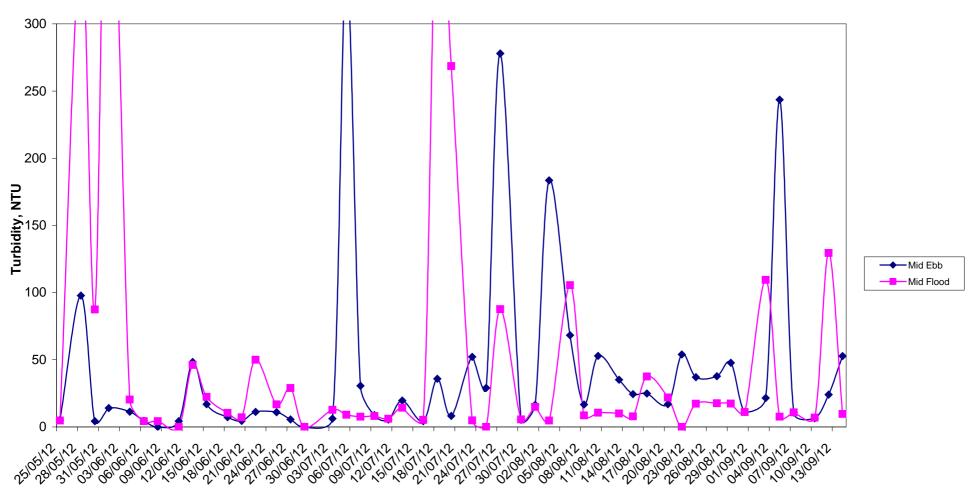


Remark: No water at C1 occasionally after 17/02/2011. Zero values are shown in the graph

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel Fax E-mail Website : +852-2450 8233 : +852-2450 6138 : matlab@fugro.com.hk : www.fugro.com




C1 - pH

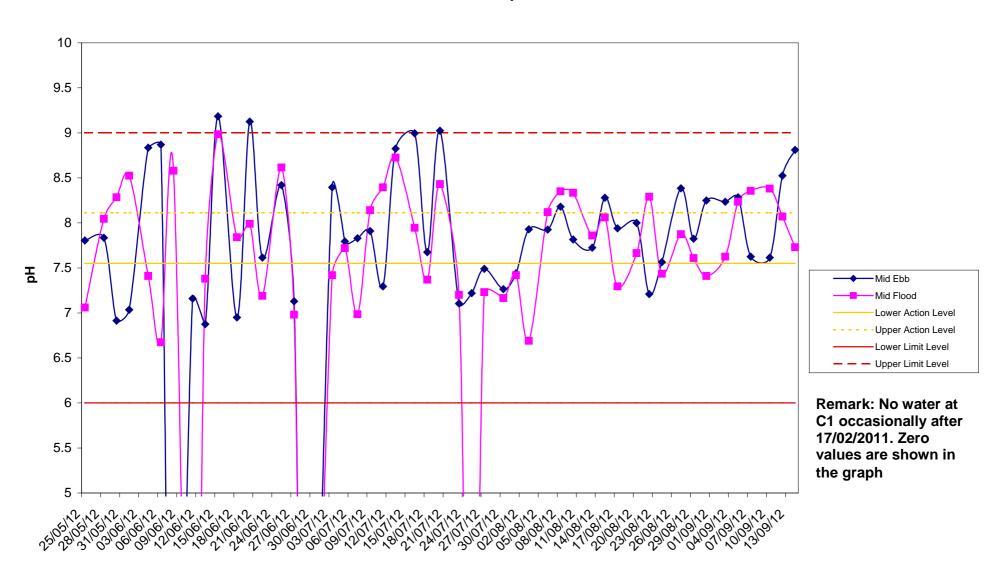

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C1 - Suspended Solids Content

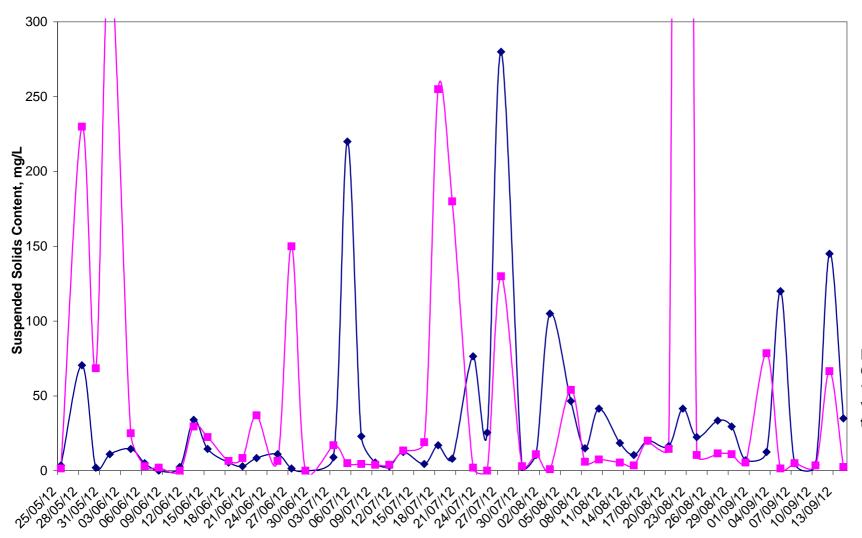




Remark: No water at C1 occasionally after 17/02/2011. Zero values are shown in the graph

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




C2 - Dissolved Oxygen Content

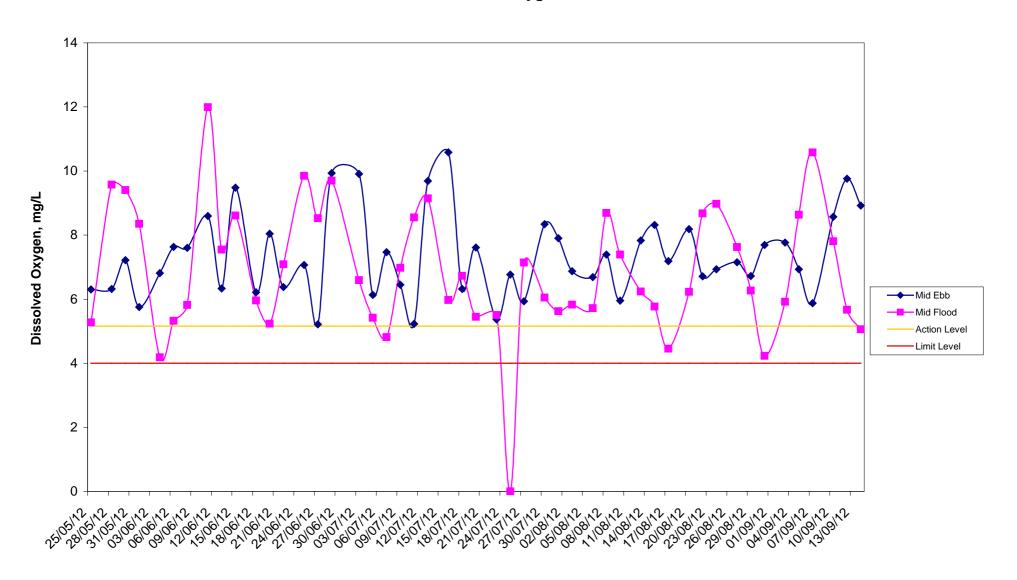

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




C2 - Turbidity

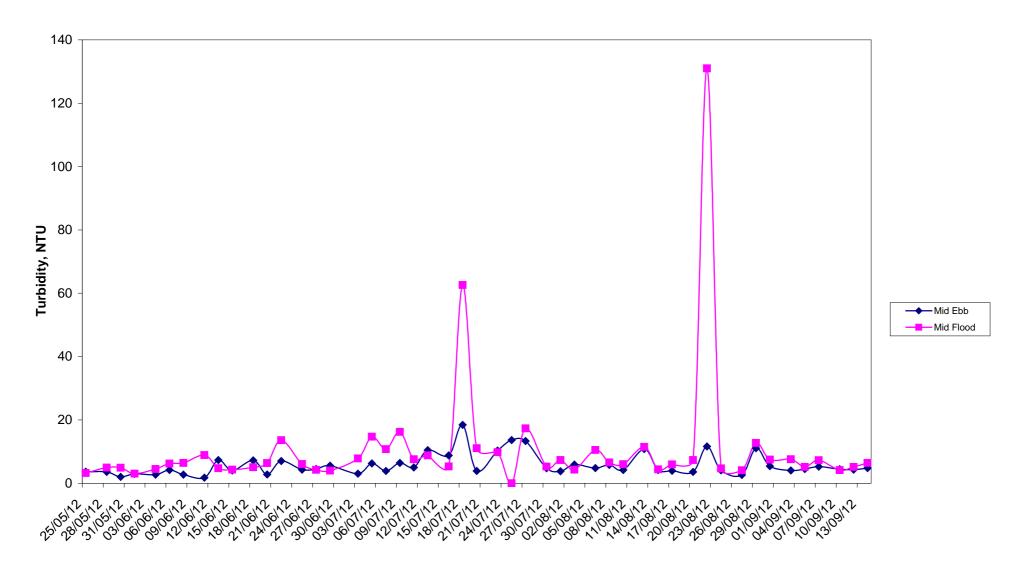

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




C2 - pH

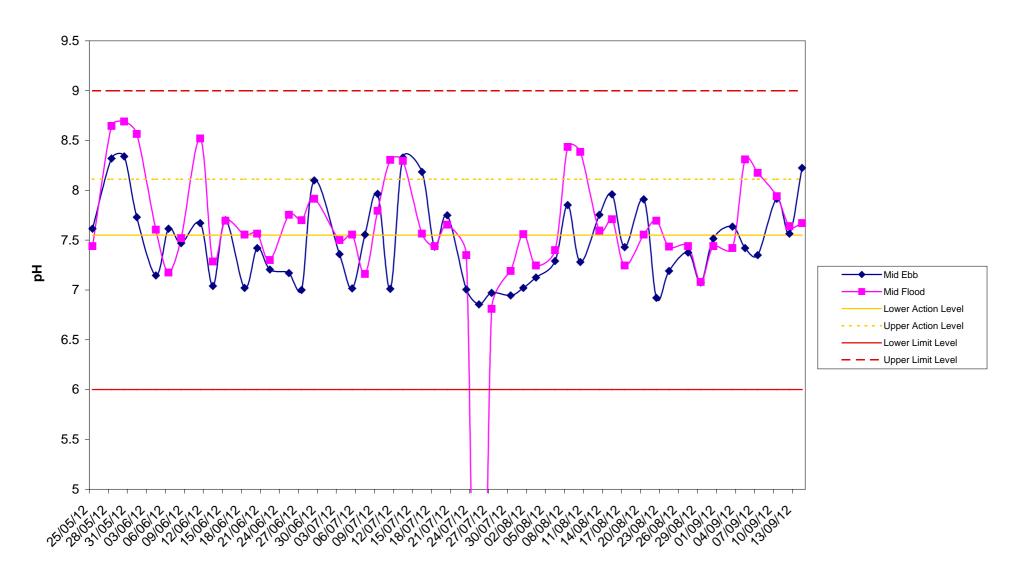

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233
Fax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



C2 - Suspended Solids Content

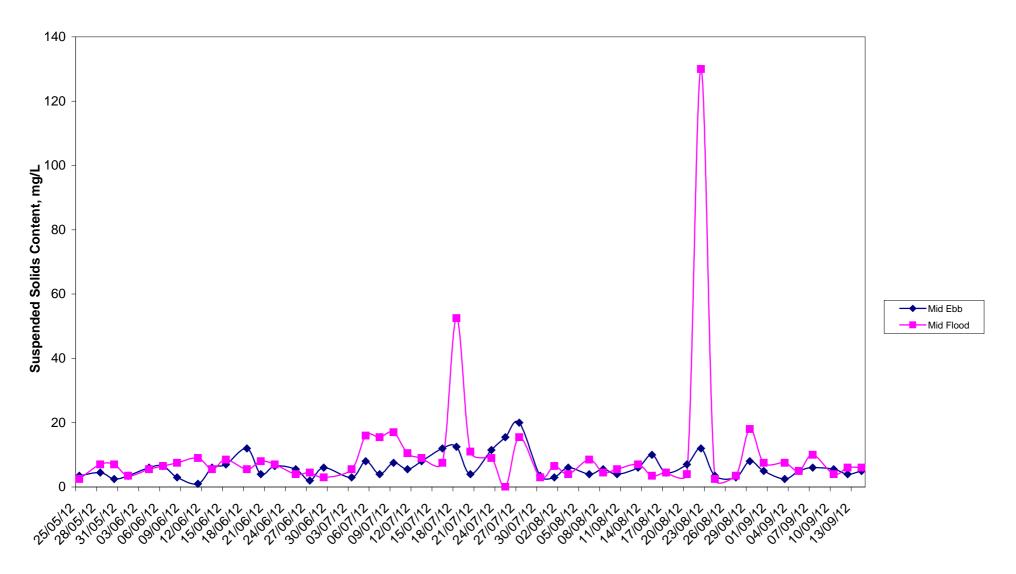

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

 Telephone
 : +852-2450 8233

 Telefax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.fugro.com



Appendix 3

Summary of Ecology Monitoring

Fugro Development Centre,

5 Lok Yi Street, Tai Lam,

Tuen Mun, N.T.,

Hong Kong.

Tel: +852-2450 8233

Fax: +852-2450 6138

: matlab@fugro.com.hk

Website: www.materialab.com.hk



Ref No.: 100440EN121502

			ug 2012 to Sept 2012	25 Sept 2012 to 24 Oct 2012			25 Oct 2012 to 24 Nov 2012	
Species Name	Scientific Name	Middle Lagoon	Notable / Breeding	Middle Lagoon	Notable / Breeding	Middle Lagoon	Notable / Breeding	
Asian Brown Flycatcher	Muscicapa dauurica	0	Activity -	1	Activity None observed	0	Activity -	
Barn Swallow	Hirundo	0	-	8	None	0	-	
Black-browed	rustica Acrocephalus	0	_	3	observed None	0	_	
Reed Warbler Black Drongo	bistrigiceps Dicrurus	0		13	observed None	0		
Black-winged	macrocercus Himantopus	3	None		observed None	_	-	
Stilt	himantopus Pycnonotus		observed None	10	observed None	0	None	
Chinese Bulbul Chinese Pond	sinensis Ardeola	8	observed None	22	observed None	40	observed	
Heron	bacchus	5	observed	1	observed	0	-	
Common Greenshank	Tringa nebularia	15	None observed	8	None observed	0	-	
Common Sandpiper	Actitis hypoleucos	3	None observed	3	None observed	0	-	
Common Snipe	Gallinago gallinago	0	-	1	None observed	0	-	
Common Stonechat	Saxicola torquata	0	-	2	None observed	1	None observed	
Crested Myna	Acridotheres cristatellus	0	-	0	-	36	None observed	
Dusky Warbler	Phylloscopus fuscatus	0	-	5	None observed	2	None observed	
Eurasian	Alauda	0	-	5	None observed	0	-	
Skylark Greater Coucal	arvensis Centropus sinensis	0	-	1	None observed	0	-	
Great Egret	Egretta alba	1	None observed	1	None observed	0	-	
Greater Sand Plover	Charadrius leschenaultii	0	-	4	None observed	0	-	
Green Sandpiper	Tringa ochropus	0	-	3	None observed	0	-	
Grey Wagtail	Motacilla cinerea	0	-	1	None observed	0	-	
Intermediate Egret	Egretta intermedia	2	None observed	5	None observed	0	-	
Japanese White-eye	Zosterops	0	-	10	None	0	-	
Kentish Plover	japonicus Charadrius	0	-	1	None observed	0	-	
Little Egret	alexandrinus Egretta	73	None	77	None	0	-	
Little Grebe	garzetta Tachybaptus ruficollis	34	observed Two active nests. Several juvenile / immature birds recorded.	42	observed Breeding activity. One active nest. Several juvenile / immature birds recorded.	2	None observed	
Little Ringed Plover	Charadrius dubius	15	Several juvenile birds observed.	18	Several Juvenile birds observed.	1	None observed	
Little Swift	Apus affinis	0	-	17	None observed	0	-	
Long-tailed Shrike	Lanius schach	1	None observed	2	None observed	0	-	
Long-toed Stint	Calidris subminuta	2	None observed	0	-	0	-	

Fugro Development Centre,

5 Lok Yi Street, Tai Lam,

Tuen Mun, N.T.,

Hong Kong.

Tel: +852-2450 8233

1: +852-2450 6138

1: matlab@fugro.com.hk

Website: www.materialab.com.hk



Ref No.: 100440EN121502

(Con't)

			ug 2012 to Sept 2012	25 Sept 2012 to 24 Oct 2012		25 Oct 2012 to 24 Nov 2012	
Species Name	Scientific Name	Middle Lagoon	Notable / Breeding Activity	Middle Lagoon	Notable / Breeding Activity	Middle Lagoon	Notable / Breeding Activity
Marsh Sandpiper	Tringa stagnatilis	34	None observed	9	None observed	0	-
Oriental Magpie Robin	Copsychus saularis	0	-	6	None observed	0	-
Oriental Reed Warbler	Acrocephalus orientalis	1	None observed	1	None observed	0	-
Pheasant-tailed Jacana	Hydrophasian us chirurgus	0	-	3	None observed	0	-
Pied Kingfisher	Ceryle rudis	3	None observed	2	None observed	0	-
Plain Prinia	Prinia inornata	2	None observed	1	None observed	0	-
Red-rumped Swallow	Hirundo daurica	0	-	1	None observed	0	-
Red Turtle Dove	Streptopelia tranquebarica	0	-	2	None observed	0	-
Red-Whiskered Bulbul	Pycnonotus jocosus	0	-	2	None observed	0	-
Temminck's Stint	Calidris temminckii	0	-	8	None observed	0	-
White Wagtail	Motacilla alba	28	None observed	34	None observed	4	None observed
Yellow-bellied Prinia	Prinia flaviventris	1	None observed	2	None observed	0	-
Yellow Wagtail	Motacilla flava	6	None observed	7	None observed	0	-
Zitting Cisticola	Cisticola juncidis	0	-	1	None observed	0	-
Total Numbers		237	3 nests	343		86	
Total Species		19		40		7	

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Appendix 4

Summary of Landscape and Visual Impact Survey

Fugro Development Centre,

5 Lok Yi Street, Tai Lam,

Tuen Mun, N.T.,

Hong Kong.

Tel: +852-2450 8233

1: +852-2450 6138

1: matlab@fugro.com.hk

Website: www.materialab.com.hk



Ref No.: 100440EN121502

				Aug 2012 to Sept 2012	25 Sept 2012 to 24 Oct 2012		25 Oct 2012 to 24 Nov 2012	
ID No.	Nature / Type	Landscape and Visual Mitigation Measures	Status	Remarks	Status	Remarks	Status	Remarks
CM 1	Design / Construction Planning	Topsoil, where identified, should be stripped and stored for reuse in the construction of the soft landscape works, where practical.	Not applicable.	Test reports will be submitted by the contractor to explore the suitability of mixing PFA into the planting soil. Suitable topsoil will be imported for planting during landscape planting phase. As per observation on site, the PFA excavated out due to site formation work had been under treatment (dehydration), and is backfilled to its original location inside the site boundary. Capping of the PFA is established to prevent spreading in air. Photographic record of PFA treatment has been shown in Table 4.11. Monthly EM&A Report of Sept 2012.	Not applicable.	Suitable topsoil will be imported for planting during landscape planting phase. As per observation on site, the PFA excavated out due to site formation work had been under treatment (dehydration), and is backfilled to its original location inside the site boundary. Capping of the PFA is established to prevent spreading in air. Photographic record of PFA treatment has been shown in Table 4.5. Monthly EM&A Report of Oct 2012.	Not applicable.	Suitable topsoil will be imported for planting during landscape planting phase. As per observation on site, the PFA excavated out due to site formation work had been under treatment (dehydration), and is backfilled to its original location inside the site boundary. Capping of the PFA is established to prevent spreading in air. Photographic record of PFA treatment has been shown in Table 4.5. Monthly EM&A Report of Nov 2012.
CM 2	Site Practice	Existing trees to be retained on site should be carefully protected during construction.	Tree felling work has commenced since the approval of Phase II tree felling application. Existing trees to be retained have been carefully protected during construction. The contractor has confirmed T758 to be retained on site and proper tree protection would be required for T758. Amendment to the tree felling application will be submitted.	Photographic record of the retained tree T758 is shown in Table 4.11. Monthly EM&A Report of Sept 2012.	Tree felling work has commenced since the approval of Phase II tree felling application. Existing trees to be retained have been carefully protected during construction. The contractor has confirmed T758 to be retained on site and proper tree protection would be required for T758. Amendment to the tree felling application will be submitted.	Photographic record of the retained tree T758 is shown in Table 4.5. Monthly EM&A Report of Oct 2012.	The contractor has confirmed T758 to be retained on site and proper tree protection would be required for T758. Amendment to the tree felling application will be submitted.	Photographic record of the rectained tree T758 is shown in Table 4.5. Monthly EM&A Report of Nov 2012.

Fugro Development Centre,

5 Lok Yi Street, Tai Lam,

Tuen Mun, N.T.,

Hong Kong.

Tel: +852-2450 8233

1: +852-2450 6138

1: matlab@fugro.com.hk

Website: www.materialab.com.hk



Ref No.: 100440EN121502

(Con't)

	(Odirt)			2012 to ot 2012	25 Sept 2012 to 24 Oct 2012		25 Oct 2012 to 24 Nov 2012	
ID No.	Nature / Type	Landscape and Visual Mitigation Measures	Status	Remarks	Status	Remarks	Status	Remarks
CM 3	Design / Construction Planning	Trees unavoidably affected by the works should be transplanted where practical.	Tree transplant work has been completed. The final transplant locations for the transplant trees will be revised. The transplant trees will be accommodated within the site area. Amendment to the tree felling application will be submitted accordingly.	The compensatory proposal already revised in the amendment to include more compensatory trees for the 3 dead transplant trees. The contractor verified on site to ensure the final location of the transplant trees will be suitable for the remaining 13 transplanted trees.	Tree transplant work has been completed. The final transplant locations for the transplant trees will be revised. The transplant trees will be accommodated within the site area. Amendment to the tree felling application will be submitted accordingly.	The compensatory proposal already revised in the amendment to include more compensatory trees for the 3 dead transplant trees. The contractor verified on site to ensure the final location of the transplant trees will be suitable for the remaining 13 transplanted trees.	Tree transplant work has been completed. The final transplant locations for the transplant trees will be revised. The transplant trees will be accommodated within the site area. Amendment to the tree felling application will be submitted accordingly.	The compensatory proposal already revised in the amendment to include more compensatory trees for the 3 dead transplant trees. The contractor verified on site to ensure the final location of the transplant trees will be suitable for the remaining 13 transplanted trees.
CM 4	Design / Construction Planning	Compensatory tree planting should be provided to compensate for felled trees.	More compensatory trees will be added for the dead transplant trees, which already reflected in the tree felling resubmission. New trees planting is proposed on the either side of the bridge at portion 6 to fulfill the EIA requirements. These shall be reflected in the revised compensatory proposal as well.	Location for the compensatory trees to be verified on site by the contractor. Photographic record is shown in Table 4.11. Monthly EM&A Report of Sept 2012.	More compensatory trees will be added for the dead transplant trees, which already reflected in the tree felling resubmission. New trees planting is proposed on the either side of the bridge at portion 6 to fulfill the EIA requirements. These shall be reflected in the revised compensatory proposal as well.	Location for the compensatory trees to be verified on site by the contractor and shown in Table 4.5. Monthly EM&A Report of Oct 2012.	More compensatory trees will be added for the dead transplant trees, which already reflected in the tree felling resubmission. New trees planting is proposed on the either side of the bridge at portion 6 to fulfill the EIA requirements. These will be reflected in the revised compensatory proposal as well.	Location for the compensatory trees to be verified on site by the contractor and shown in Table 4.5. Monthly EM&A Report of Nov 2012.
CM 5	Site Practice	Control of night- time lighting.	In progress.	Night-time work was implemented from 7pm to 11pm for certain period in Sept 2012. The lighting is confined to the construction site without affecting the periphery area. Photographic record of the night-time working is shown in Table 4.11. Monthly EM&A Report of Sept 2012.	In progress.	Night-time work was implemented from 7pm to 6am for certain period in Oct 2012. The lighting is confined to the construction site without affecting the periphery area. Photographic record of the night-time working is shown in Table 4.5. Monthly EM&A Report of Oct 2012.	In progress.	Night-time work was implemented from 7pm to 6am for certain period in November 2012. The lighting is confined to the construction site without affecting the periphery area. Photographic record of the night-time working is shown in Table 4.5. Monthly EM&A Report of Nov 2012.
CM 6	Design / Construction Planning	Erection of decorative screen hoarding compatible with the surrounding setting.	Completed.	Erection of decorative screen hoarding has been set up along the site boundary.	Completed.	Erection of decorative screen hoarding has been set up along the site boundary.	Completed.	Erection of decorative screen hoarding has been set up along the site boundary.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Appendix 5

Summary of Waste Flow

Fugro Development Centre, Tel : +852-2450 8233 5 Lok Yi Street, Tai Lam, Fax : +852-2450 6138 Tuen Mun, N.T., E-mail : matlab@fugro.com.hk Hong Kong. Website : www.materialab.com.hk



Ref No.: 100440EN121502

Summary of Waste Flow

Type of Waste	Quantity Generated in September 2012	Quantity Generated in October 2012	Quantity Generated in November 2012
Inert C&D Waste*	4,079.547m ³	1,357.284m ³	139.984m ³
Chemical Waste (Liquid)	NIL	NIL	NIL
Chemical Waste (Solid)	NIL	940.000kg	NIL
Metal	43,035.750kg	19,955.000kg	46,720.000kg
Paper / Cardboard Packaging	935.500kg	941.000kg	1,159.500kg
Plastic	960.000kg	80.000kg	10.000kg
Others, e.g. General Refuse	182.838m ³	137.044m ³	169.888m ³

Remarks: Density of Inert C&D waste and general refuse is 1.9 tonne/m³ and 1.6 tonne/m³ respectively

The total quantity generated of Insert C&D Waste in April and May 2012 were revised as the quantities of reused in other projects need to be included.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Appendix 6

Event Action Plan for Water Quality Monitoring

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Event/Action Plan for Water Quality

Event	ET Leader	IEC	SOR	Contractor
Action level being exceeded by one sampling day	Repeat in situ measurement to confirm findings; Identify reasons for non-compliance and source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Repeat measurement on next day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly; Assess the effectiveness of the implemented mitigation measures.	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. Assess the effectiveness of the implemented mitigation measures.	Inform the SOR and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and SOR; Implement the agreed mitigation measures.
Action level being exceeded by more than one consecutive sampling day	Repeat in situ measurement to confirm findings; Identify reasons for non-compliance and source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor;	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly; Assess the effectiveness of the implemented mitigation measures.	Discuss with IEC on the Proposed mitigation measures; Make agreement on the mitigation measures to be implemented; ◆ Assess the effectiveness of the implemented mitigation measures.	Inform the SOR and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and SOR within three working days;

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Event	ET Leader	IEC	SOR	Contractor
Limit level being exceeded by one sampling day	Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; Repeat measurement on next day of exceedance. Repeat in situ measurement to confirm findings; Identify reasons for non-compliance and source(s) of impact; Inform IEC Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, SOR and Contractor; Ensure mitigation measures are implemented; Increase the monitoring	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the SOR accordingly; Assess the effectiveness of the implemented mitigation measures.	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures.	Implement the agreed mitigation measures. Inform the SOR and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plar and equipment; Consider changes of working methods; Discuss with ET, IEC and SOR and propose mitigation measures to IEC and SOR within three working days; Implement the agreed mitigation measures.
Limit level being exceeded by more than one	frequency to daily until no exceedance of Limit level. Repeat in situ measurement to confirm	Discuss with ET and Contractor on	Discuss with IEC, ET and Contractor on	Inform the SOR and confirm
consecutive sampling day	findings; • Identify reasons for	the mitigation measures; • Review	the proposed mitigation measures;	notification of the non- compliance in

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Event	ET Leader	IEC	SOR	Contractor
	and source(s) of impact; Inform IEC Contractor and EPD; • Check monitoring data, all plant, equipment and Contractor's working methods; • Discuss mitigation measures with IEC, SOR and Contractor; • Ensure mitigation measures are implemented; • Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.	measures submitted by Contractor and advise the SOR accordingly; • Assess the effectiveness of the implemented mitigation measures.	critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level.	unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and SOR and propose mitigation measures to IEC and SOR within three working days; Implement the agreed mitigation measures; As directed by the SOR, to slow down or to stop all or part of the construction activities.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




Appendix 7

Figures

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com




Figure 1.1
WENT Landfill Consultation Zone

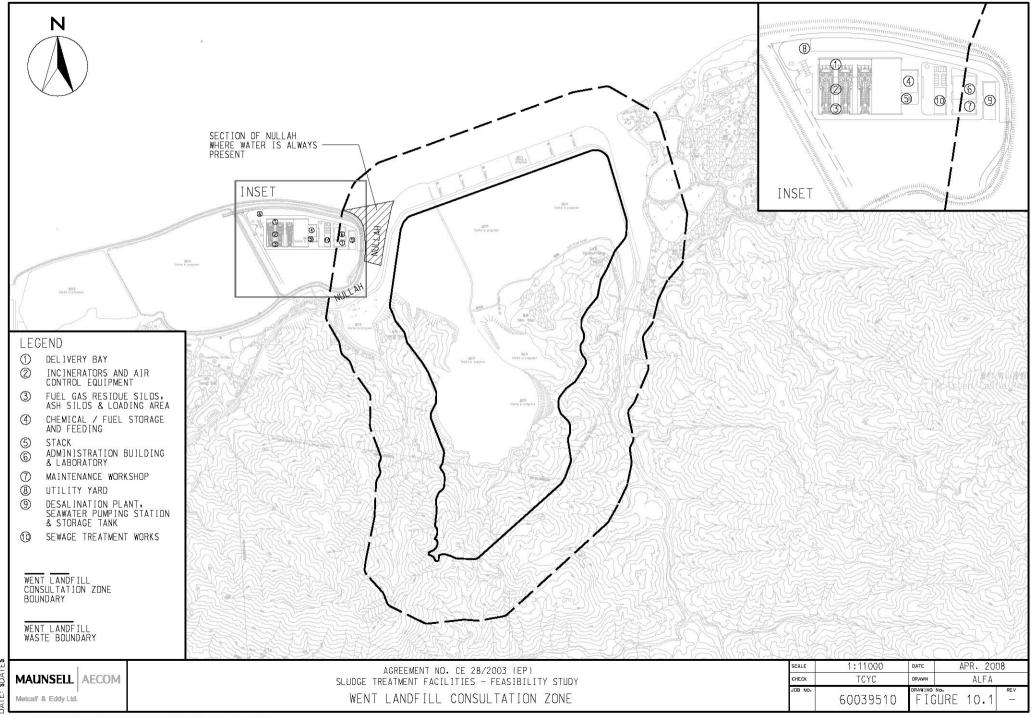

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Figure 3.1 Location of Project Site

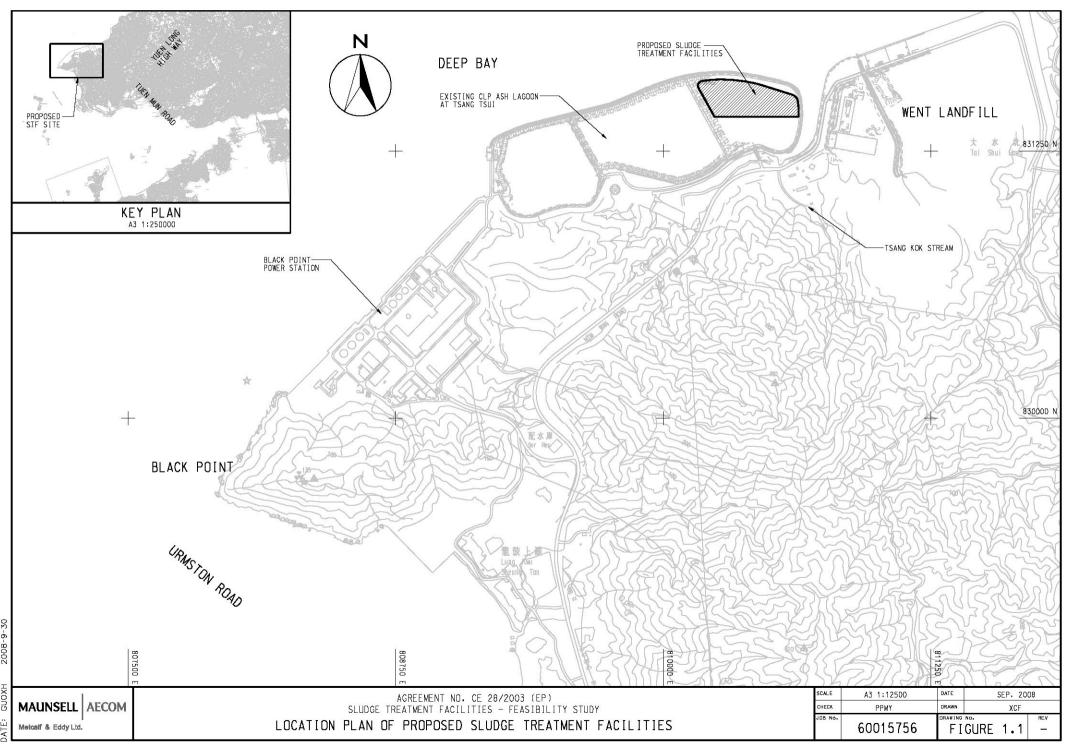

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com

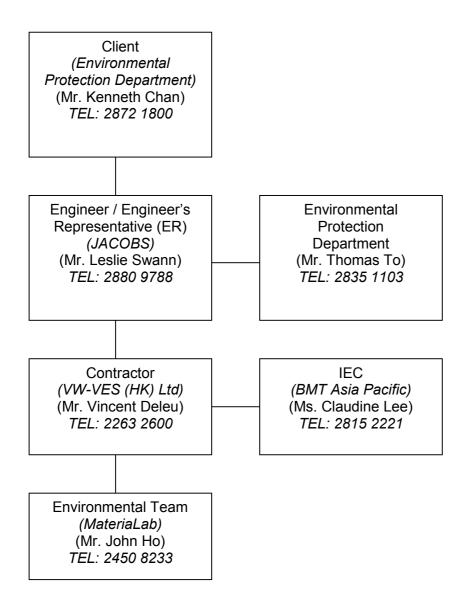


Figure 3.2 Project Organisation Structure

MateriaLab Division, Tel : +852-2450 8233
Fugro Development Centre, Fax : +852-2450 6138
5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Website : www.materialab.com.hk




Management Structure and Organization Chart




MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Figure 4.1 - 4.2
Water Quality Monitoring Location

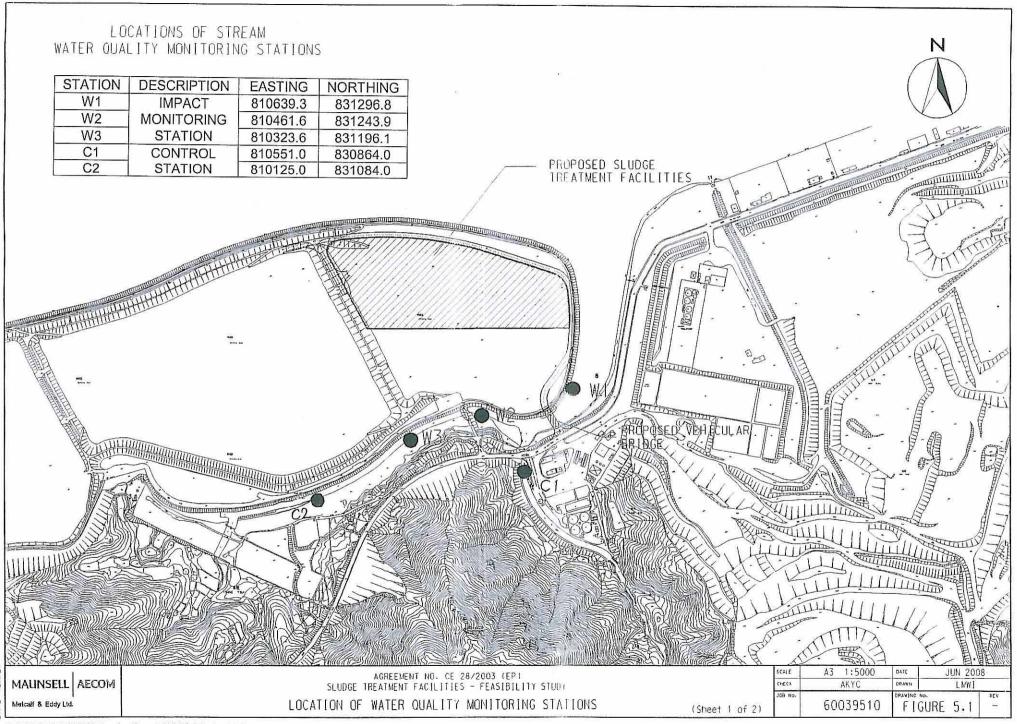

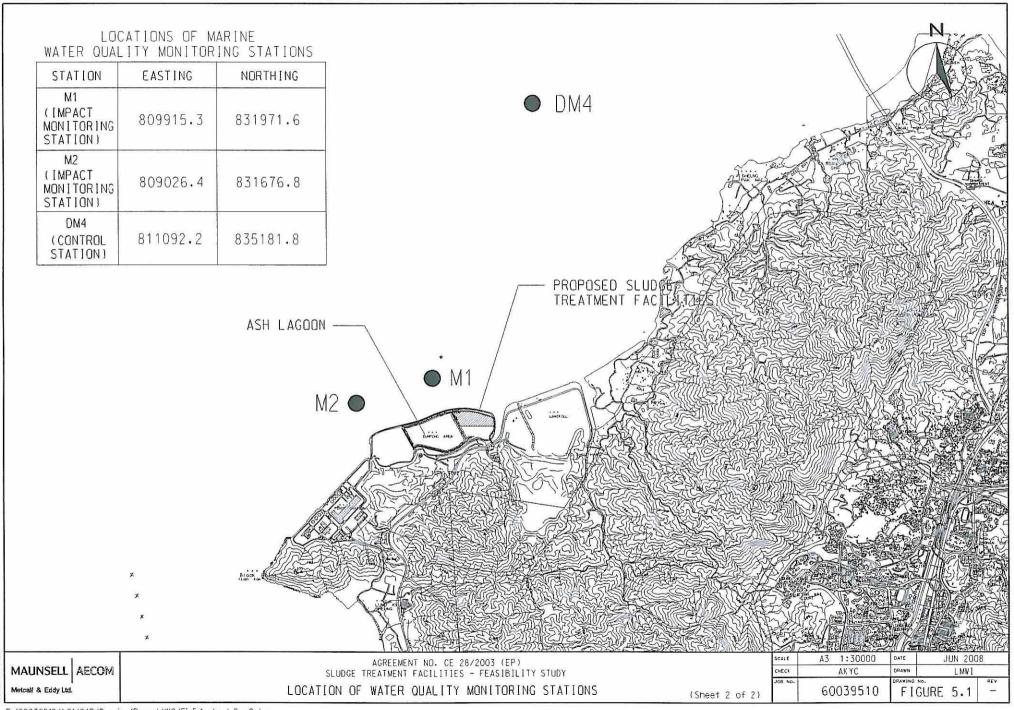

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Telephone : +852-2450 8233
Telefax : +852-2450 6138
E-mail : matlab@fugro.com.hk
Website : www.fugro.com



Appendix 8

Work Program

