

The Jockey Club CPS Limited

Central Police Station Conservation  
and Revitalisation Project:  
*Thirteenth Monthly EM&A Report*  
*(1 November to 30 November 2012)*

Issue Date: December 2012

**Environmental Resources Management**

16/F

DCH Commercial Centre  
25 Westlands Road  
Quarry Bay, Hong Kong  
Telephone: (852) 2271 3000  
Facsimile: (852) 2723 5660  
E-mail: [post.hk@erm.com](mailto:post.hk@erm.com)  
<http://www.erm.com>

The Jockey Club CPS Limited

Central Police Station Conservation  
and Revitalisation Project:  
*Thirteenth Monthly EM&A Report*  
*(From 1 November to 30 November*  
*2012)*

Issue Date: December 2012

Reference 0095646

For and on behalf of	
ERM-Hong Kong, Limited	
Approved by:	Frank Wan
Signed:	
Position:	Partner
Certified by:	
	(Environmental Team Leader – Winnie Ko)
Date:	12 December 2012

This report has been prepared by ERM-Hong Kong, Limited with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client.

We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.

This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies on the report at their own risk.

Your ref. 0095646\_let\_Atkins\_20121217 Monthly EM&A Report No.13.doc  
Our ref. 4690/OC039/SO

Telephone (852) 2972 1000  
Facsimile (852) 2890 6343

info.hk@atkinsglobal.com  
www.atkinsglobal.com

Date: 17 December 2012

**By Fax (2723 5660) and Post**

ERM-Hong Kong Limited,  
21/F Lincoln House,  
979 King's Road,  
Taikoo Place, Island East,  
Hong Kong

**Attn: Ms Winnie Ko**

Dear Winnie,

**Central Police Station Conservation and Revitalization Project  
Verification of Monthly EM&A Report No.13**

We refer to your letter dated 17 December 2012 regarding the Monthly EM&A Report No.13. Atkins China Ltd. verifies, in the capacity of Independent Environmental Checker, that the report, in principle, conforms the requirements provided in Condition 3.4 of the Environmental Permit (EP-408/2011/B).

**Yours sincerely,  
For Atkins China Ltd.**



**Sharifah Or  
Independent Environmental Checker**

c.c. Mr. KOH Say Wee, HKJC  
Mr. Charles Kung, Rocco Design Architect

Fax: 2504 2903  
Fax: 2529 2135

## CONTENTS

1	INTRODUCTION	1
1.1	PURPOSE OF THE REPORT	1
1.2	STRUCTURE OF THE REPORT	1
2	PROJECT INFORMATION	3
2.1	BACKGROUND	3
2.2	SITE DESCRIPTION	3
2.3	CONSTRUCTION ACTIVITIES	3
2.4	PROJECT ORGANISATION	4
2.5	STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS	4
3	ENVIRONMENTAL MONITORING REQUIREMENTS	6
3.1	NOISE MONITORING	6
3.1.1	Monitoring Location	6
3.1.2	Monitoring Parameters, Frequency and Programme	6
3.1.3	Monitoring Equipment and Methodology	6
3.1.4	Event / Action Plan	7
3.1.5	Mitigation Measures	7
3.2	CULTURAL HERITAGE	8
3.2.1	Vibration Monitoring	8
3.2.2	Mitigation Measures	9
3.3	LANDSCAPE AND VISUAL MONITORING	9
3.3.1	Mitigation Measures	9
3.4	ENVIRONMENTAL REQUIREMENTS IN CONTRACT DOCUMENTS	9
4	IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS	10
5	MONITORING RESULTS	11
5.1	NOISE	11
5.2	CULTURAL HERITAGE	11
5.3	LANDSCAPE AND VISUAL	12
5.4	WASTE MANAGEMENT	12
6	ENVIRONMENTAL SITE INSPECTION	14
7	ENVIRONMENTAL NON-CONFORMANCE	15
7.1	SUMMARY OF MONITORING EXCEEDANCE	15
7.2	SUMMARY OF ENQUIRY	15
7.3	SUMMARY OF ENVIRONMENTAL NON-COMPLIANCE	15
7.4	SUMMARY OF ENVIRONMENTAL COMPLAINT	15
7.5	SUMMARY OF ENVIRONMENTAL SUMMONS AND SUCCESSFUL PROSECUTION	17

8	<b>FUTURE KEY ISSUES</b>	18
8.1	<b>KEY ISSUES FOR THE COMING MONTH</b>	18
8.2	<b>MONITORING SCHEDULE FOR THE NEXT MONTH</b>	18
8.3	<b>CONSTRUCTION PROGRAMME FOR THE NEXT MONTH</b>	18
9	<b>CONCLUSIONS</b>	19

#### **LIST OF TABLES**

<b>Table 2.1</b>	<b>Summary of Construction Activities Undertaken from 1 November to 30 November 2012</b>
<b>Table 2.2</b>	<b>Summary of Environmental Licensing, Notification and Permit Status</b>
<b>Table 3.1</b>	<b>Construction Phase Noise Monitoring Station</b>
<b>Table 3.2</b>	<b>Noise Monitoring Equipment</b>
<b>Table 3.3</b>	<b>Action and Limit Levels for Construction Noise Monitoring</b>
<b>Table 3.4</b>	<b>Alert, Alarm and Action (AAA) Levels for Vibration Monitoring</b>
<b>Table 3.5</b>	<b>Event and Action Plan for Vibration Monitoring</b>
<b>Table 4.1</b>	<b>Status of Required Submissions</b>
<b>Table 5.1</b>	<b>Findings of Monthly Tree Inspection in the Reporting Period</b>
<b>Table 5.2</b>	<b>Quantities of Waste Generated from the Project</b>
<b>Table 7.1</b>	<b>Summary of Complaints Received</b>
<b>Table 8.1</b>	<b>Construction Works to be Undertaken in the Coming One Month</b>

#### **LIST OF ANNEXES**

<b>Annex A</b>	<b>Locations of Works Areas and the Surroundings</b>
<i>Annex A1</i>	<i>Project Location</i>
<i>Annex A2</i>	<i>Declared Monuments within the Project Site</i>
<i>Annex A3</i>	<i>Site Layout Plan marked with Works</i>
<b>Annex B</b>	<b>Project Organization Chart and Contact Detail</b>
<b>Annex C</b>	<b>Locations of Noise Monitoring Stations and Noise Sensitive Receivers</b>
<b>Annex D</b>	<b>Monitoring Schedule of the Reporting Month and the Next Month</b>
<b>Annex E</b>	<b>Calibration Reports for Calibrators and Sound Level Meters</b>
<b>Annex F</b>	<b>Event /Action Plans for Noise</b>
<b>Annex G</b>	<b>Summary of Implementation Status</b>
<b>Annex H</b>	<b>Noise Monitoring Results</b>
<b>Annex I</b>	<b>Construction Programme for the Project</b>

- Annex J**     **Tree Inspection Reports**
- Annex K**     **Environmental Complaint, Environmental Summons and  
Prosecution Log**
- Annex L**     **Records of Vibration Monitoring for Trial Piling and Pipe /  
Bored Piling Works**
- Annex M**     **Records of Vibration Monitoring for Other Construction  
Works**

## EXECUTIVE SUMMARY

The construction works of **Central Police Station Conservation and Revitalisation Project** commenced on 24 October 2011. This is the thirteenth monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A works carried out during the period from 1 November to 30 November 2012 in accordance with the EM&A Manual.

### Summary of Construction Works undertaken during Reporting Period

The major construction works undertaken during the reporting period include:

- Trial pile loading test near Block 14;
- Demolition and excavation works at Block 8;
- Ground improvement (grouting) works at Block 17;
- Pipe pile walls piling works at Old Bailey Wing (Block 50);
- Metal scaffolding erection at Block 11 and Block 12;
- Protection works of Tree 5; and
- Air duct and E&M removal works at Block 1.

### Environmental Monitoring and Audit Progress

A summary of the monitoring activities in this reporting period is listed below:

- |   |          |
|---|----------|
| • Construction noise monitoring during normal weekdays at each monitoring station | 6 times  |
| • Joint environmental site inspection   | 1 time   |
| • Joint heritage site inspection  | 1 time   |
| • Landscape & visual monitoring   | 1 time   |
| • Tree inspection   | 1 time   |
| • Vibration monitoring for trial piling works                                     | 26 times |
| • Vibration monitoring for pipe pile/bored pile walls piling works                | 26 times |
| • Vibration monitoring for other construction works                               | 26 times |

### Noise

6 sets of 30-minute construction noise measurements were carried out at each of the monitoring stations (NM2 and NM6) during normal weekdays of the reporting period. No exceedance of Limit Level of construction noise was recorded during the reporting period. An exceedance of Action Level of noise was recorded during the reporting period. An investigation was carried out to identify the cause of the exceedance.

### Cultural Heritage

26 vibration monitoring were undertaken for the trial piling works near Block 17 and the construction of pipe pile walls at Old Bailey Wing (Block 50) at

their respective monitoring locations during the reporting period. In addition, 26 vibration monitoring were carried out for the internal demolition and excavation works at Block 8 in November. No exceedance of the Alert, Alarm and Action Levels was recorded during the reporting period.

Heritage site audit was conducted on 15 November 2012. Guano was observed on the verandah of Barrack Block and the Contractor was recommended to enhance the polythene sheet protection to floors and to carry out cleaning of guano daily as agreed. A scaffold pole was touching the revetment wall below the north elevation of D Hall (Block 14) and it was rectified by the Contractor immediately. Also, protection is required to the doors on the North Balconies of Block 1, as well as the southwest corner of B Hall (Block 12) to protect brickwork.

The follow-up actions recommended in the October audit have generally been implemented.

#### Landscape & Visual

Landscape and visual monitoring has commenced since October 2011 on a monthly basis. Tree inspection was conducted on 1 November 2012 by the arborist during the reporting period. The Contractor was recommended to continue to monitor the planters for any signs of new cracks. Drooping branches and leaves observed in Tree 6 during the last site inspection have been removed. The Contractor was reminded to remove the drooping branches and leaves in Tree 7 as well.

#### Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. A total of 843.86 tonnes of inert C&D materials were generated during the reporting period. 47.44 tonnes of non-inert C&D materials comprising general refuse were generated and disposed of at the SENT Landfill. 5,650 kg of metals were produced and were sent to recyclers for recycling. No paper/cardboard packaging, plastics waste or chemical waste was generated during the reporting period.

#### Environmental Site Inspection

A joint environmental site inspection was carried out by the representatives of the Contractor, the IEC and the ET on 15 November 2012. There was no non-compliance recorded during the site inspection. Details of the audit finding are presented in *Section 6*.

#### Environmental Exceedance/Non-conformance/Compliant/Summons and Prosecution

No exceedance of Limit Level of construction noise was recorded at designated monitoring stations during the reporting period. An exceedance



of Action Level of noise was recorded during the reporting period. An investigation was carried out.

No exceedance of the Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

One enquiry was received during the reporting period.

No non-compliance event was recorded during the reporting period.

Two complaints were received during the reporting period.

No summons/prosecution was received during the reporting period.

#### Future Key Issues

Works to be undertaken in the next month include:

- Trial pile loading test;
- Grout curtain at Old Bailey Wing (Block 50);
- Ground improvement works at Block 17;
- Underpinning / demolition works at Block 8;
- Structural open up investigation at Block 17;
- General strip out works at Block 1;
- Archaeological watch brief works at Arbuthnot Wing; and
- Pipe pile wall construction at Parade Ground.

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoff and waste management.

ERM-Hong Kong, Limited (ERM) was appointed by the Jockey Club CPS Limited (the CPS Ltd) as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme for the **Central Police Station Conservation and Revitalisation Project** (the Project).

### **1.1 PURPOSE OF THE REPORT**

This is the thirteenth EM&A report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from **1 November** to **30 November 2012**.

### **1.2 STRUCTURE OF THE REPORT**

The structure of the report is as follows:

Section 1 : **Introduction**

details the scope and structure of the report.

Section 2 : **Project Information**

summarises background and scope of the Project, site description, project organization and contact details, construction programme, the construction works undertaken and the status of Environmental Permit(s)/License(s) during the reporting period.

Section 3 : **Environmental Monitoring Requirements**

summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, Event/ Action Plans, environmental mitigation measures as recommended in the EIA report and relevant environmental requirements.

Section 4 : **Implementation Status on Environmental Protection Requirements**

summarises the implementation of environmental protection measures during the reporting period.

Section 5 : **Monitoring Results**

summarises the monitoring results obtained in the reporting period.

Section 6 : **Environmental Site Inspection**

summarises the audit findings of the weekly site inspections undertaken within the reporting period.

Section 7: **Environmental Non-conformance**

summarises any monitoring exceedance, environmental complaints and environmental summons within the reporting period.

Section 8: **Future Key Issues**

summarises the impact forecast and monitoring schedule for the next reporting month.

Section 9: **Conclusions**

## 2 PROJECT INFORMATION

### 2.1 BACKGROUND

The Chief Executive (CE)'s 2007-2008 Policy Address highlighted revitalisation as the guiding principle of heritage conservation and the Project was one of the specific proposals put forward by the CE in the same Policy Address. At the meeting of the Executive Council (ExCo) on 15 July 2008, the ExCo advised and the CE ordered that Government should enter into a partnership with the Hong Kong Jockey Club (HKJC) in the form of an agreement (or agreements) to take forward the conservation and revitalisation of the CPS project based on various guiding parameters. The Project is now being undertaken in partnership with the Development Bureau of the HKSAR Government. The HKJC has taken on board the decision at the ExCo meeting and further investigated the design and implementation of the Project. The Project is now implemented by the CPS Limited.

### 2.2 SITE DESCRIPTION

The location of the Project Site is shown in *Annex A1*. The Site is bounded by Hollywood Road to the north, Arbuthnot Road to the east, Chancery Lane to the south and Old Bailey Street to the west.

The Site comprises three Declared Monuments designated under the *Antiquities and Monuments Ordinance* in 1995. They are:

- Central Police Station;
- Former Central Magistracy; and
- Victoria Prison Compound.

They are collectively named the Central Police Station (CPS). *Annex A2* shows the location of the Declared Monuments within CPS and the buildings within the CPS.

### 2.3 CONSTRUCTION ACTIVITIES

A summary of the major construction activities undertaken in this reporting period is shown in *Table 2.1* and illustrated in *Annex A3*.

**Table 2.1** *Summary of Construction Activities Undertaken from 1 November to 30 November 2012*

<b>Construction Activities Undertaken</b>
<ul style="list-style-type: none"> <li>• Trial pile loading test near Block 14;</li> <li>• Demolition and excavation works at Block 8;</li> <li>• Ground improvement (grouting) works at Block 17;</li> <li>• Pipe pile walls piling works at Old Bailey Wing (Block 50);</li> <li>• Metal scaffolding erection at Block 11 and Block 12;</li> <li>• Protection works of Tree 5; and</li> <li>• Air duct and E&amp;M removal works at Block 1.</li> </ul>

**2.4** *PROJECT ORGANISATION*

The Project organisation chart and contact details are shown in *Annex B*.

**2.5** *STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS*

A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project since the granting of the EP in April 2011 is presented in *Table 2.2*.

**Table 2.2** *Summary of Environmental Licensing, Notification and Permit Status*

<b>Permit/ Licences/ Notification</b>	<b>Reference</b>	<b>Validity Period</b>	<b>Remarks</b>
Environmental Permit (EP)	EP-408/2011	-	Superseded on 10 January 2012
	EP-408/2011/A	-	Superseded on 22 March 2012
	EP-408/2011/B	Throughout the Contract	Permit granted on 22 March 2012
Notification of Construction Works as required under <i>Air Pollution Control (Construction Dust) Regulation</i>	Ref. No. 332920	Throughout the Contract	-
Registration of Waste Producer under <i>Waste Disposal Ordinance</i>	Waste Producer No.: 5213-122-G2347-25	Throughout the Contract	-
Effluent Discharge License under <i>Water Pollution Control Ordinance</i>	License No. WT00010633-2011	21 Oct 2011 – 31 Oct 2016	-
Notification of Commencement of Asbestos Abatement Work under <i>Air Pollution Control Ordinance</i>	-	Throughout the Contract	EPD's letter (EPD's ref.: (5) in EPAC/A/4/000/23 3 II) dated 2 December 2011 satisfied that the

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
			content of the asbestos abatement plan (Report No.: 0210/11/ED/0078A ) is in accordance with the APCO
Approval of Asbestos Abatement Work (Phase 2)	-	Earliest commencement date on 26 January 2012	EPD's letter (EPD's ref:() in EPAC/A/4/000/233) dated 18 January 2012.
Construction Noise Permit (CNP)	GW-RS0734-12	11 July 2012 at 0200 hours to 2 August 2012 at 0400 hours	Expired.
	GW-RS0839-12	13 August 2012 at 1900 hours to 31 December 2012 at 0700 hours	-
	GW-RS1162-12	1 December 2012 at 0000 hours to 28 March 2013 at 0600 hours	-

### 3.1 NOISE MONITORING

#### 3.1.1 Monitoring Location

The construction noise monitoring locations are listed in *Table 3.1* and are shown in *Annex C*.

**Table 3.1 Construction Phase Noise Monitoring Station**

Monitoring Location	Proposed Construction Noise Monitoring Station			
	ID in EM&A Manual	ID	Type of Measurement	Remark
Rooftop of Ho Fook Building	N2	NM2	Façade	-
Rooftop of Chancery Mansion	---	NM6	Façade	Accesses to the original proposed monitoring location in the EM&A Manual, Chancery House (N5), were denied; alternative location of Chancery Mansion (N6), were therefore proposed and approved by the Authorised Person (AP), the Independent Environmental Checker (IEC) and EPD.

The noise sensitive receivers are also shown in *Annex C*.

#### 3.1.2 Monitoring Parameters, Frequency and Programme

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. The monitoring programme for this reporting period is shown in *Annex D*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ) in decibels dB(A).  $L_{eq(30min)}$  were used as the monitoring parameter for the time period in between 0700 – 1900 hours on normal weekdays. Supplementary information for data auditing, two statistical sound levels  $L_{10}$  and  $L_{90}$  - the levels exceeded for 10 and 90 percent of the time respectively, were also recorded during the monitoring for reference. The measured noise levels were logged in every 5 minutes throughout the impact monitoring period.

#### 3.1.3 Monitoring Equipment and Methodology

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures of Technical Memorandum on Noise from Construction Work other than Percussive Piling (GW-TM)* issued under the *Noise Control Ordinance (NCO) (Cap 400)*.

The sound level meters and calibrator used for the noise measurement, as listed in *Table 3.2*, complies with the IEC 651: 1979 and 804:1985 (Type 1) specifications. The calibration certificates of the sound level meters are appended in *Annex E*.

**Table 3.2** *Noise Monitoring Equipment*

Monitoring Stations	Monitoring Equipment (Sound Level Meter and Calibrator)
NM2, NM6	<u>Calibrator</u> Rion NC-73 (S/N 10997142)
	<u>Sound Level Meter</u> Rion NL-31 (S/N 00603867)

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

Measurements were accepted as the calibration level from before and after the noise measurement agree to within 1.0 dB(A).

### 3.1.4 *Event / Action Plan*

**Table 3.3** *Action and Limit Levels for Construction Noise Monitoring*

Noise Monitoring Location	Action Level	Limit Level, $L_{eq}(30mins), dB(A)$	Remark
NM2, NM6	When one documented complaint is received from any one of the sensitive receivers	75 (note)	Applicable during 0700 – 1900 hours on normal weekdays.

Notes:

- Acceptable Noise Levels for Area Sensitivity Rating of A/B/C. Limit Level is reduced to 70dB(A) for schools and 65dB(A) during school examination periods.
- If works are to be carried out during restricted hours, the conditions stipulated in the CNP issued by the NCA have to be followed.

The Event / Action Plan (EAP) for noise monitoring is presented in *Annex F*.

### 3.1.5 *Mitigation Measures*

The mitigation measures in accordance with the EP, EIA and EM&A Manual and their implementation status are presented in *Annex G*.

## 3.2 *CULTURAL HERITAGE*

### 3.2.1 *Vibration Monitoring*

In accordance with the EM&A Manual, vibration monitoring is required and the vibration control limits and vibration monitoring proposal are defined by a specialist for AMO's approval.



### *Baseline Monitoring*

A set of initial readings should be recorded prior to commencement of each stage of demolition works or trial piling works. The baseline vibration monitoring should be conducted for duration of 5 minutes on the measurement day(s) at each vibration monitoring location.

### *Vibration Monitoring for Demolition Works*

There are five phases/stages of vibration monitoring to be carried out for demolition works, namely Initial Reading Phase, Monitoring Stage 1, Monitoring Stage 2, Monitoring Stage 3 and Monitoring Stage 4. The monitoring location is shown in *Annex L*. The vibration monitoring should be conducted for duration of 5 minutes on the days with demolition works at each vibration monitoring location.

### *Vibration Monitoring for Trial Piling and Pipe/Bored Piling Works*

Vibration monitoring for trial piling works and pipe/bored piling works is required. The monitoring location is shown in *Annex L*. The vibration monitoring should be conducted for duration of 5 minutes on the days with trial piling works or pipe/bored piling works at each vibration monitoring location.

### *Vibration Monitoring for Other Construction Works*

Vibration monitoring for specific construction works other than demolition works, trial piling works and pipe/bored piling works is also required in accordance with Building Department's requirement. The monitoring location is shown in *Annex M*. The number and location of monitoring location will depend on the location of the specific construction works. The vibration monitoring should be conducted for duration of 5 minutes on a daily basis (working day) at each vibration monitoring location.

### *Alert, Alarm and Action Levels*

The Alert, Alarm and Action (AAA) Levels are to be implemented during the vibration monitoring and shown in *Table 3.4*.

**Table 3.4** *Alert, Alarm and Action (AAA) Levels for Vibration Monitoring*

<b>Instrument Type</b>	<b>Item Monitored</b>	<b>Alert Level</b>	<b>Alarm Level</b>	<b>Action Level</b>
Vibration Monitoring	Horizontal Movement	2.0 mm/s	2.5 mm/s	3.0 mm/s

The Event / Action Plan (EAP) for vibration monitoring is shown in *Table 3.5*.

**Table 3.5** *Event and Action Plan for Vibration Monitoring*

<b>Events</b>	<b>Action</b>
Exceedance of Alert Level	Notify Management Contractor
Exceedance of Alarm Level	Notify Authorised Person/ Resident Engineer
Exceedance of Action Level	Cease Works and submit mitigation

**3.2.2** *Mitigation Measures*

Cultural heritage mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

**3.3** *LANDSCAPE AND VISUAL MONITORING*

In accordance with the EM&A Manual, inspections of affected trees were conducted by an experienced and appropriately trained arborist. All irregularities that deviate from the recommended tree protection measures or could impose deleterious impacts on the protected trees were reported. Besides, implementation of mitigation measures for landscape and visual resources recommended in the EIA Report were also monitored during the site inspection.

**3.3.1** *Mitigation Measures*

Landscape and visual mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

**3.4** *ENVIRONMENTAL REQUIREMENTS IN CONTRACT DOCUMENTS*

The environmental requirements as specified in the contract documents were reviewed and were covered in the EIA's requirements.

## **IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS**

The Contractor has generally implemented the environmental mitigation measures and requirements as stated in the EIA Report, the EP and EM&A Manual and the contract documents. The implementation status during the reporting period is summarized in *Annex G*.

Status of required submissions under the EP during the reporting period is presented in *Table 4.1*.

**Table 4.1**      *Status of Required Submissions*

<b>Submission</b>		<b>Submission Date</b>
<i>EP Condition</i>		
Condition 3.4	Twelfth Monthly EM&A Report	14 November 2012

## 5 *MONITORING RESULTS*

### 5.1 *NOISE*

A total of 6 sets of 30-minute construction noise measurements were carried out at the monitoring stations (NM2 and NM6) during normal weekdays of the reporting period. The monitoring results together with graphical presentations are presented in *Annex H*. The local impacts observed near the monitoring stations of NM2 and NM6 were summarised below:

- NM2: construction noise from activities in the Project Site and traffic noise from Old Bailey Street.
- NM6: construction noise from activities in the Project Site and traffic noise from Chancery Lane.

No exceedance of Limit Level of construction noise was recorded during the reporting period. An exceedance of Action Level of noise (complaint received) was recorded during the reporting period. The investigation was carried out and findings are presented in *Section 7.4*.

### 5.2 *CULTURAL HERITAGE*

#### 5.2.1 *Vibration Monitoring*

26 vibration monitoring measurements for the trial piling works near Block 17 were carried out in November. The monitoring results are presented in *Annex L*.

26 vibration monitoring measurements were undertaken for the construction of pipe pile walls at the Old Bailey Wing (Block 50) during the reporting period. The monitoring results are presented in *Annex L*.

26 vibration monitoring measurements were carried out for the demolition and excavation works at Block 8 during the reporting period. The monitoring results are presented in *Annex M*.

All monitoring results were below the Alert/Alarm/Action Levels.

#### 5.2.2 *Heritage Site Audit*

Monthly heritage site audit was conducted on 15 November 2012 by the Heritage Checker and the observations are summarised below:

1. Guano was observed on the verandah of the Barrack Block. The Contractor was recommended to enhance the polythene sheet protection to floors and to carry out cleaning of guano daily as agreed.

2. A scaffold pole was touching the revetment wall below the north elevation of D Hall (Block 14). It was rectified by the Contractor immediately.
3. Protection is required to the southwest corner of B Hall (Block 12) to protect the brickwork.
4. Protection to the doors on North Balconies of Block 1 is required.

The follow-up actions recommended in the October audit have generally been implemented.

### 5.3 LANDSCAPE AND VISUAL

The tree inspection was conducted by the arborist on 1 November 2012 and major observations and recommendations in the reporting period are summarised in *Table 5.1*. The tree inspection report is contained in *Annex J*.

**Table 5.1 Findings of Monthly Tree Inspection in the Reporting Period**

Tree No.	Botanical Name	Overall Health Condition	Arborist's Observations / Recommendations
Tree -5	<i>Mangifera indica</i>	Good	<ul style="list-style-type: none"> <li>• No further action required.</li> </ul>
Tree -6	<i>Aleurites moluccana</i>	Fair	<ul style="list-style-type: none"> <li>• To check for any signs of new crack weekly;</li> <li>• The drooping branches and leaves have been trimmed on 1 November 2012.</li> </ul>
Tree-7	<i>Aleurites moluccana</i>	Fair	<ul style="list-style-type: none"> <li>• To check for any signs of new crack weekly;</li> <li>• To remove the remaining drooping branches and leaves.</li> </ul>
Tree-8	<i>Plumeria rubra</i>	Fair	<ul style="list-style-type: none"> <li>• No further action required.</li> </ul>
Tree-9	<i>Araucaria cunninghamia</i>	Fair	<ul style="list-style-type: none"> <li>• No further action required.</li> </ul>
Tree-11	<i>Dracaena marginata</i>	Fair	<ul style="list-style-type: none"> <li>• No further action required.</li> </ul>

### 5.4 WASTE MANAGEMENT

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. Non-inert C&D materials were made up of wastes such as general refuse. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting period are summarised in *Table 5.2*. The non-inert C&D materials and general refuse generated from the Project were disposed of at the SENT Landfill. 5,650 kg of metals were generated

and sent to recyclers for recycling. No paper/cardboard packaging, plastics waste or chemical waste was generated during the reporting period.

**Table 5.2 Quantities of Waste Generated from the Project**

Month / Year	Quantity						
	C&D Materials (inert) <sup>(a)</sup>	C&D Materials (non-inert) <sup>(b)</sup>	Chemical Waste		Recycled materials		
			Solid	Liquid	Paper / cardboard	Plastics	Metals
November 2012	843.86 tonnes	47.44 tonnes	0 kg	0 L	0 kg	0 kg	5,650 kg

**Notes:**

- (a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil.
- (b) The figure presented under non-inert C&D materials represents quantities of non-recyclable materials such as general refuse which were disposed of at SENT Landfill. Recycled materials are reported separately.

Joint environmental site inspection was conducted by the representatives of the Contractor, IEC and the ET in the reporting period on 15 November 2012. There was no non-compliance recorded during the site inspection.

*Follow-up Actions for the Last Site Audit*

Handling of metal materials was not observed in the open area near Block 3.

*Observations and Recommendations of this Reporting Month*

- 1) Steel collars for noise reduction were not installed to some of the hand-held breakers for the slab demolition works at Block 8. The Contractor was recommended to provide steel collars to all the hand-held breakers;
- 2) Considerable noise was emitted from the operating air compressor near Block 14. The Contractor was advised to enclose the air compressor with acoustic mat; and
- 3) A few oil drums were observed being stored without a drip tray near Block 14. The Contractor was reminded to put the oil drums on a drip tray to prevent potential land contamination if oil spillage occurred.

## 7 ENVIRONMENTAL NON-CONFORMANCE

### 7.1 SUMMARY OF MONITORING EXCEEDANCE

An exceedance of Action Level of noise was recorded during the reporting period. An investigation has been undertaken and additional mitigation measures have been undertaken. No exceedance of Limit Level of construction noise or Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

### 7.2 SUMMARY OF ENQUIRY

One enquiry was received during the reporting period. An email enquiry from a nearby resident was received by the Lands Department, which was later referred to the Development Bureau and transferred to JCCPS on 22 November 2012. The enquirer mentioned that the construction works at the medium level of Old Bailey Street were being carried out during early morning time (i.e. 0730 hrs) and requested for a timetable/completion date of the construction works at the location. JCCPS will send a draft reply to the Development Bureau for review and Development Bureau will then provide a formal reply to the enquirer.

### 7.3 SUMMARY OF ENVIRONMENTAL NON-COMPLIANCE

No non-compliance event was recorded during the reporting period.

### 7.4 SUMMARY OF ENVIRONMENTAL COMPLAINT

Two complaints were received during the reporting period. A complaint about noise nuisance was received by Gammon Construction Limited (GCL) on 15 November 2012. Another complaint about smell nuisance was received by the EPD and transferred to GCL on 23 November 2012.

*Table 7.1 Summary of Complaints Received*

<b>Date of Complaint Received by the Contractor</b>	<b>Means by which complaint was received</b>	<b>Nature of complaint</b>
15 November 2012	Gammon Construction Limited (Contractor)	Noise nuisance
23 November 2012	Environmental Protection Department	Smell nuisance

On 15 November 2012 at 1010 hrs, GCL has received a complaint on noise nuisance generated from the construction site at around 0730 hrs for a duration of about 15 minutes. According to the information provided by the Contractor, relocation of piling machine was carried out near Block 8 at about 0730 hrs on 15 November 2012. Other major construction activities undertaken on 15 November included slab demolition works at Block 8 and



grouting works at Block 17, both commenced at around 0900 hrs. The noise nuisance indicated by the complainant was likely resulted from the movement of the piling machine against the inclined steel platform during the relocation works. Subsequent to the receipt of the noise complaint, it has been agreed with the Contractor that the relocation of piling machine will be carried out, as far as possible, at the end of the working day instead of during early morning time. The Contractor has been reminded to ensure that acoustic curtains are properly installed prior to conducting the piling machine relocation. Additionally, the Contractor has been advised to notify all workers and operation supervisor about the complaint on 15 November 2012 and to remind them to minimise noise generation as far as possible during the relocation of the piling machine as well as other construction work activities.

On 23 November 2012, GCL received a complaint transferred from the EPD with regard to nuisance from operating machinery emissions. The complainant living along Chancery Lane mentioned that diesel smell was perceived at his location and suspected that the emissions were originated from the construction site. According to the information provided by the Contractor, the diesel exhaust emissions may be generated by the following operating plant in the vicinity of Chancery Lane on 23 November 2012:

- Three operating air compressors near Block 14;
- An operating mobile crane near Block 17; and
- Three drilling machines being operated concurrently during the grouting works at the north elevation of Block 17.

It has been confirmed with GCL that all on-site machineries are using Ultra-Low Sulphur Diesel (ULSD) and that diesel is directly filled into the machinery. There is no on-site storage of diesel oil. However, exhaust emissions from the above diesel-powered mechanical equipment may be dispersed beyond the construction site boundary, potentially affecting nearby residents along Chancery Lane.

The Contractor has been recommended to implement measures to direct the diesel exhaust emissions away from the nearby sensitive receivers as far as practicable, particularly residents along Chancery Lane (to the south and Old Bailey Street) to the west of the construction site. As reported by the Contractor, a number of mitigation measures have been implemented to facilitate the dispersion of the exhaust emissions:

- 1) Two ventilation fans have been installed near the exhaust of the air compressors where the exhaust emissions are directed towards the open space at Arbuthnot Wing via an air duct;
- 2) A ventilation fan has been installed to the exhaust of each of the three drilling machines on the north elevation of Block 17. The ventilation fans were connected to air ducts which divert the exhaust emissions to the north towards the Old Bailey Wing; and

- 3) The exhaust of the mobile crane was connected to an air duct through which the emissions were filtered by a drum filled with water.

Furthermore, the Contractor has been reminded to monitor any irregular and excessive exhaust emissions from all operating plant. The Contractor should ensure that there is no oil leakage from all operating machineries and provide drip trays, where applicable. Additionally, the Contractor has been reminded to ensure that all mitigation measures as reported are properly implemented prior to operating any PME that is likely to generate considerable exhaust emissions. The Contractor has also been advised to notify all workers and operation supervisor of the emission complaint on 23 November.

The complaint investigation reports and the cumulative number of complaints are presented in *Annex K*.

## 7.5

### *SUMMARY OF ENVIRONMENTAL SUMMONS AND SUCCESSFUL PROSECUTION*

No summons was received during the reporting period.

**8.1 KEY ISSUES FOR THE COMING MONTH**

Works to be undertaken for the coming monitoring period are summarised in *Table 8.1*.

**Table 8.1 Construction Works to be Undertaken in the Coming Month**

---

**Work to be Undertaken**


---

- Trial pile loading test;
  - Grout curtain at Old Bailey Wing (Block 50);
  - Underpinning / demolition works at Block 8;
  - Ground improvement works at Block 17;
  - Structural open up investigation at Block 17;
  - General strip out works at Block 1;
  - Archaeological watching brief works at Arbuthnot Wing; and
  - Pipe pile wall construction at Parade Ground.
- 

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoff and waste management.

**8.2 MONITORING SCHEDULE FOR THE NEXT MONTH**

The tentative schedule of noise monitoring for the next reporting period is presented in *Annex D*.

**8.3 CONSTRUCTION PROGRAMME FOR THE NEXT MONTH**

The most updated construction programme for the Project is presented in *Annex I*.

## CONCLUSIONS

The *Environmental Monitoring and Audit (EM&A) Report* presents the EM&A works undertaken during the period from 1 November to 30 November 2012 in accordance with EM&A Manual and the requirement under EP-408/2011/B.

No exceedance of Limit Level of construction noise was recorded at designated monitoring stations during the reporting period. An exceedance of Action Level of noise was recorded during the reporting period.

No exceedance of the Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

One enquiry was received during the reporting period.

No non-compliance event was recorded during the reporting period.


Two complaints were received during the reporting period.

No summons/prosecution was received during the reporting period.

The ET will keep track on the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Annex A

## Locations of Works Areas and the Surroundings

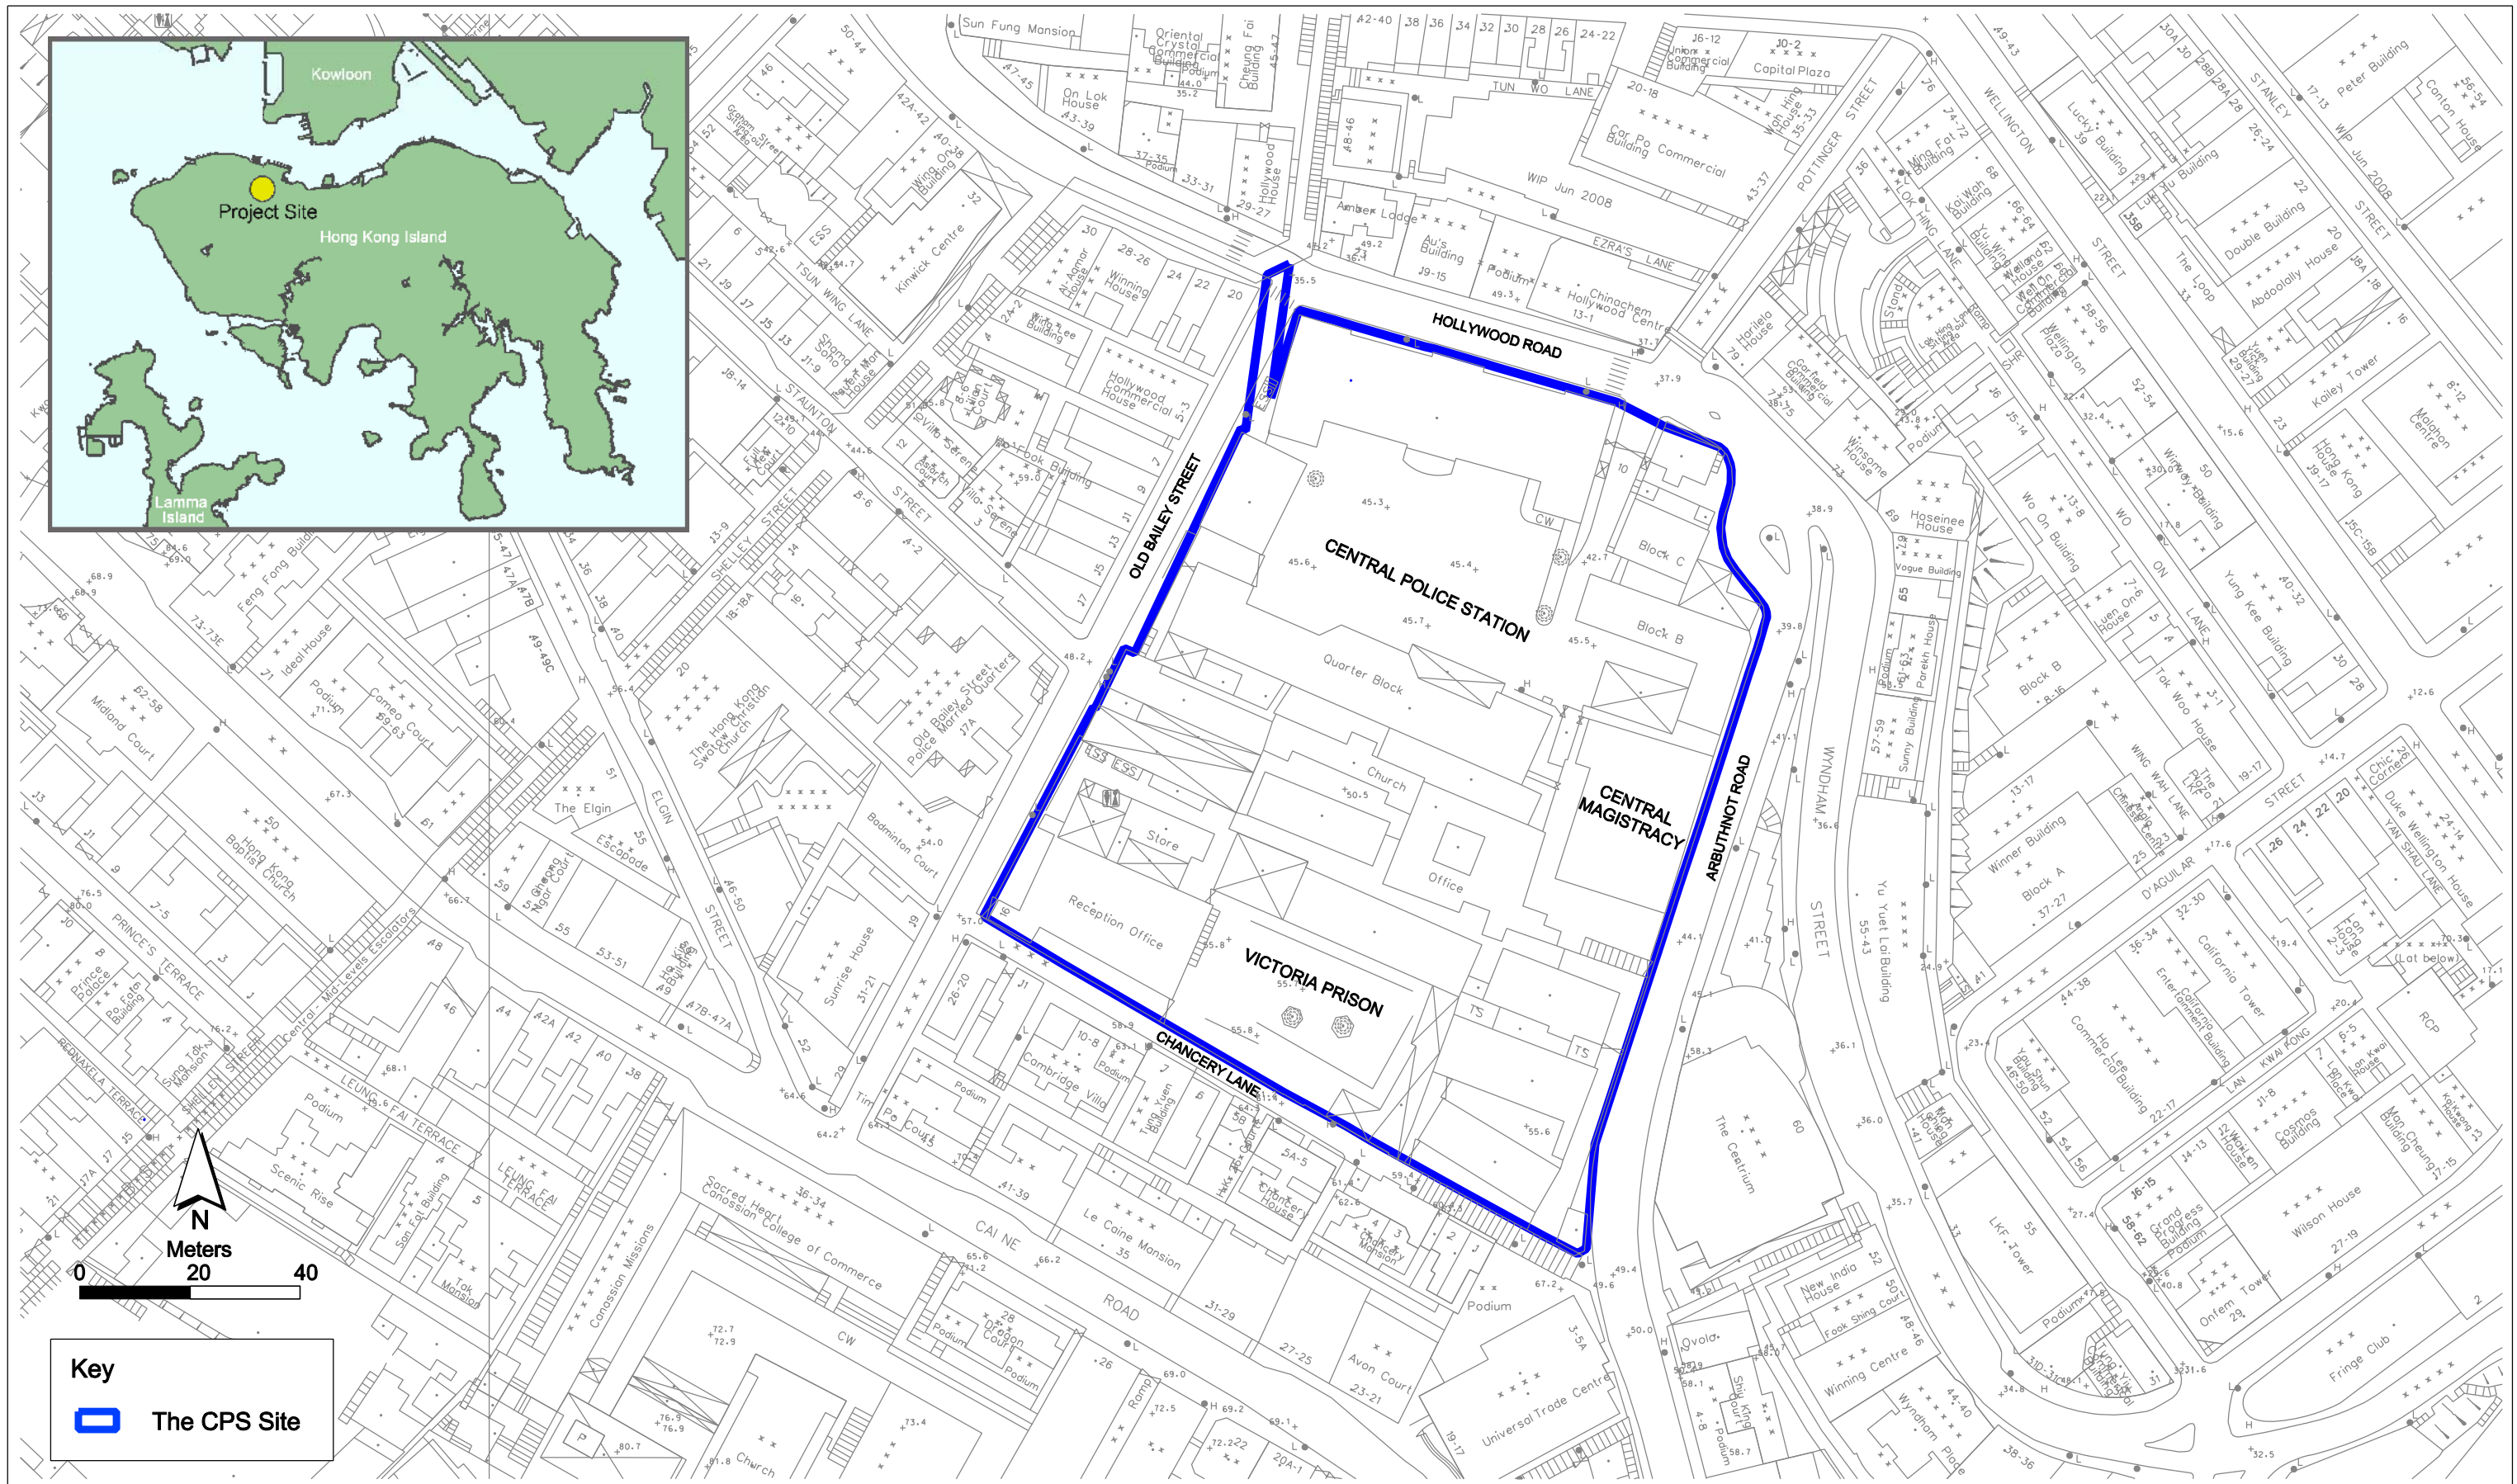


Annex A1

Project Location

**Environmental  
Resources  
Management**



**賽馬會文物保育有限公司**  
The Jockey Club CPS Limited

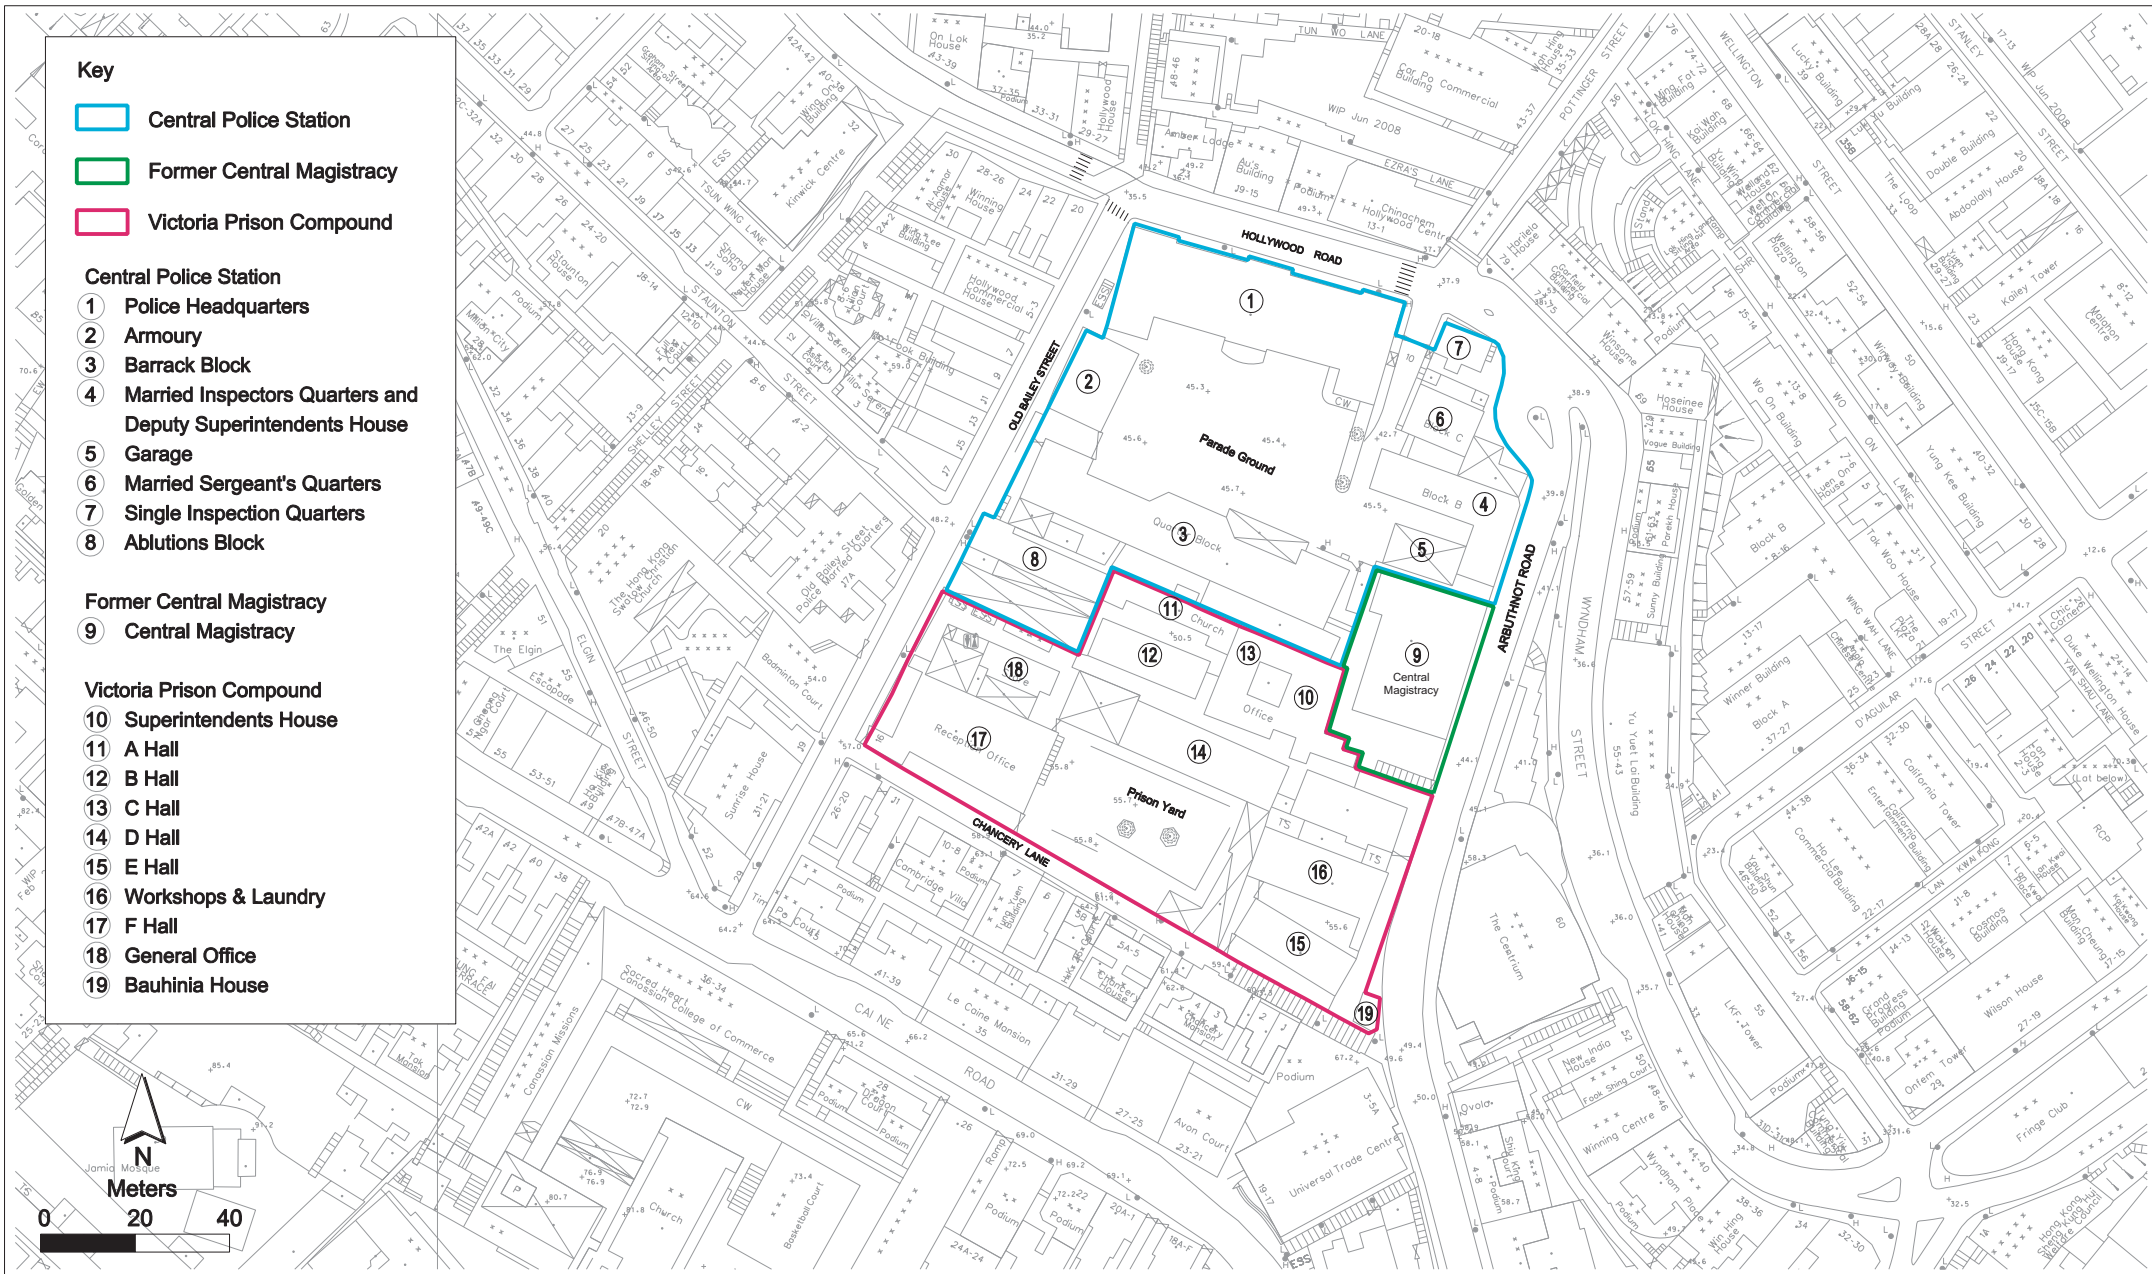

- Key**
- Central Police Station
  - Former Central Magistracy
  - Victoria Prison Compound
- Central Police Station**
- ① Police Headquarters
  - ② Armoury
  - ③ Barrack Block
  - ④ Married Inspectors Quarters and Deputy Superintendents House
  - ⑤ Garage
  - ⑥ Married Sergeant's Quarters
  - ⑦ Single Inspection Quarters
  - ⑧ Ablutions Block
- Former Central Magistracy**
- ⑨ Central Magistracy
- Victoria Prison Compound**
- ⑩ Superintendents House
  - ⑪ A Hall
  - ⑫ B Hall
  - ⑬ C Hall
  - ⑭ D Hall
  - ⑮ E Hall
  - ⑯ Workshops & Laundry
  - ⑰ F Hall
  - ⑱ General Office
  - ⑲ Bauhinia House



Annex A2

Declared Monuments within the Project Site

**Environmental Resources Management**




賽馬會文物保育有限公司  
The Jockey Club CPS Limited

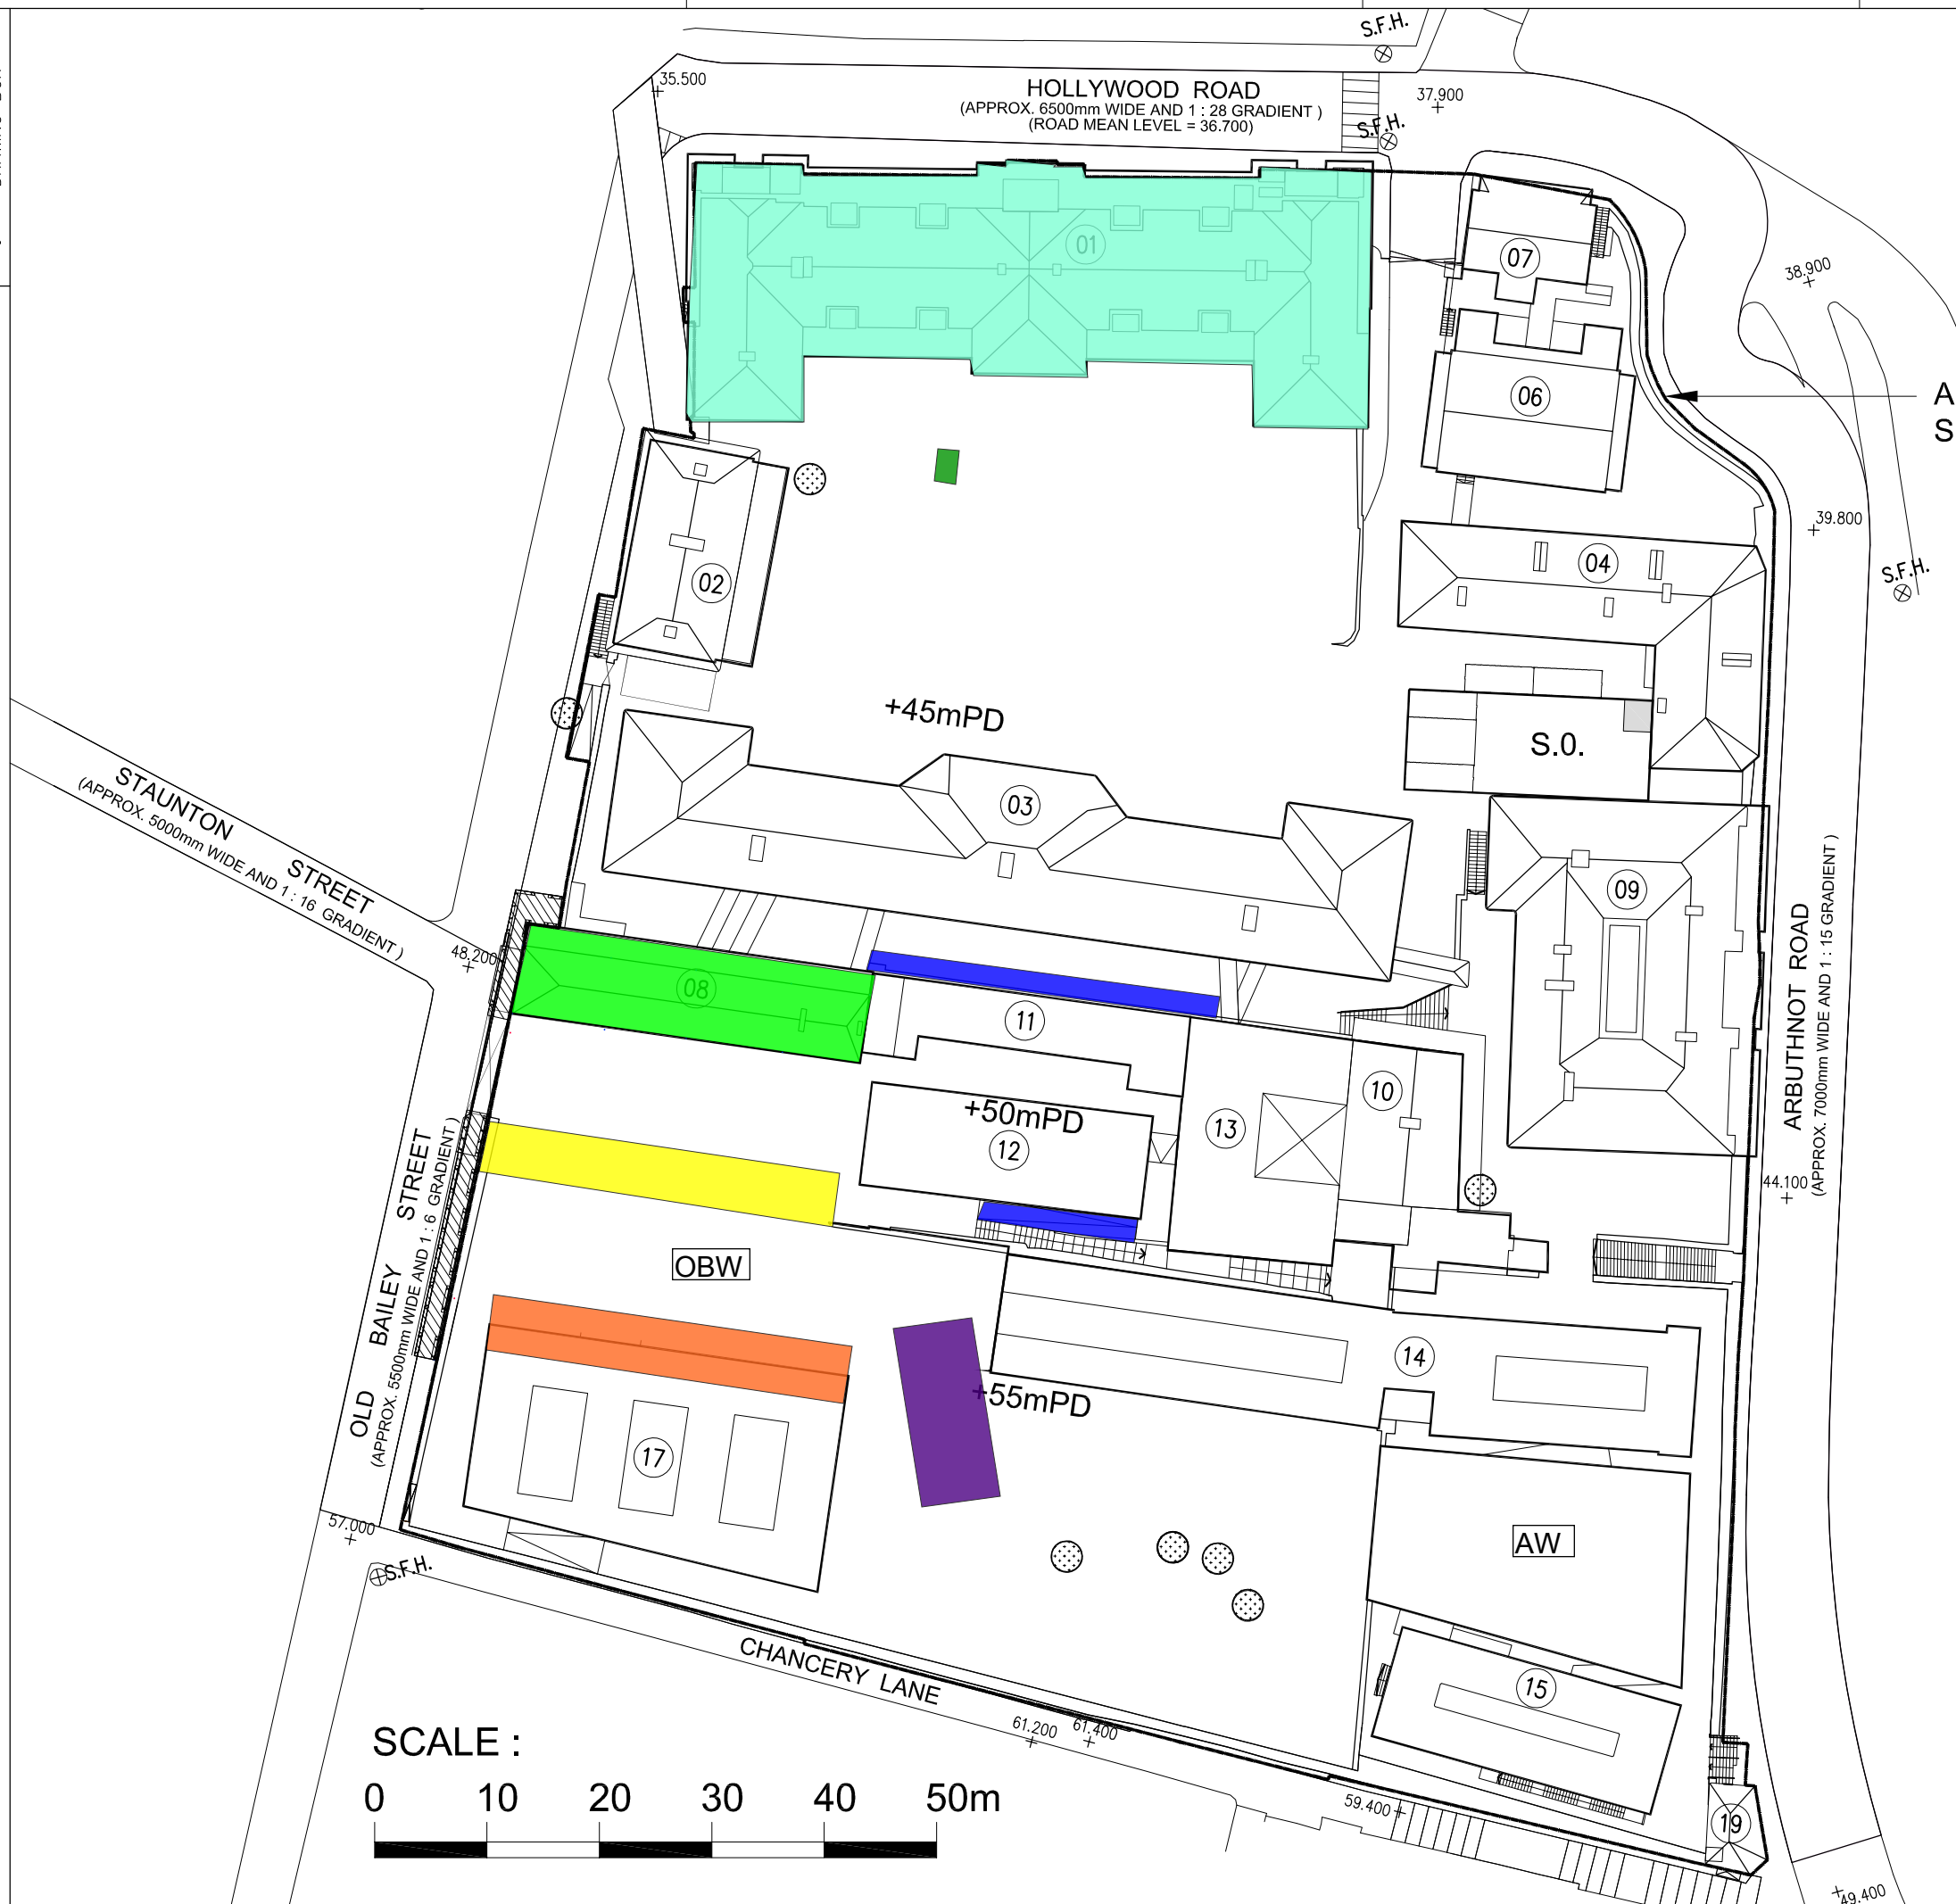

APPLICATION SITE BOUNDARY

**LEGEND**

- 1. Air Duct and E&M Removal Works
- 2. Protection Works of Tree 5
- 3. Metal Scaffold Erection
- 4. Pipe Pile Wall Piling Works
- 5. Excavation Works
- 6. Loading Test of Trial Piles
- 7. Ground Improvement Works



© Gammon Construction Limited  
This document and the copyright in it is the property of Gammon Construction Limited. Gammon Construction Limited shall forthwith take all appropriate action against any infringer of its copyright.

**CENTRAL POLICE STATION**

Client  
 賽馬會文物保育有限公司  
 The Jockey Club CPS Limited

Contractor

Drawing Title  
**SITE LAYOUT PLAN**


Drawn	Scale	N.T.S.
Designed	Status	Marked for Enquiry & Complaint log (CPS/E&C/09)
Checked		
Approved	Drawing No.	-
CAD Ref		-

**Annex A3 Site Layout Plan marked with Works (November - 2012)**



Annex B

## Project Organization Chart and Contact Detail

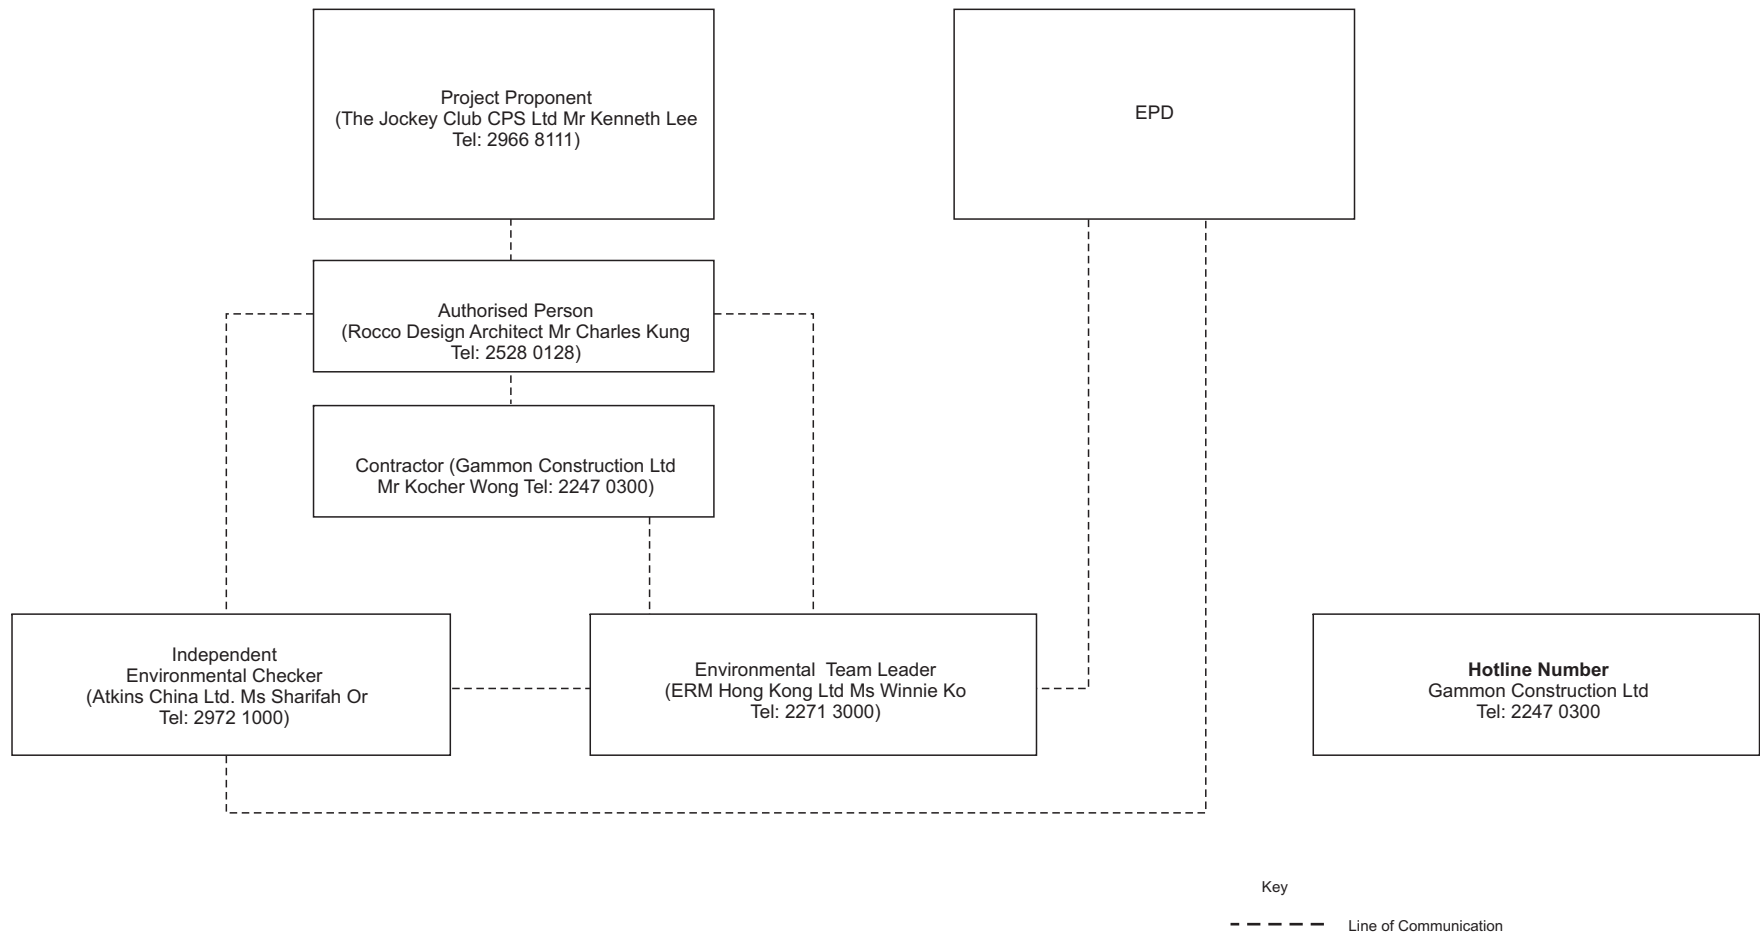

Annex C



Locations of Noise  
Monitoring Stations and  
Noise Sensitive Receivers

**Key**

- Representative Noise Sensitive Receiver
- ▭ Project Site

NSR	Description
N1	Amber Lodge
N2	Ho Fook Building
N3	Old Bailey Street Police Married Quarters
N4	Cambridge Villa
N5	Chancery House
N6	Chancery Mansion


Noise Monitoring Locations	
NM2	Ho Fook Building
NM6	Chancery Mansion

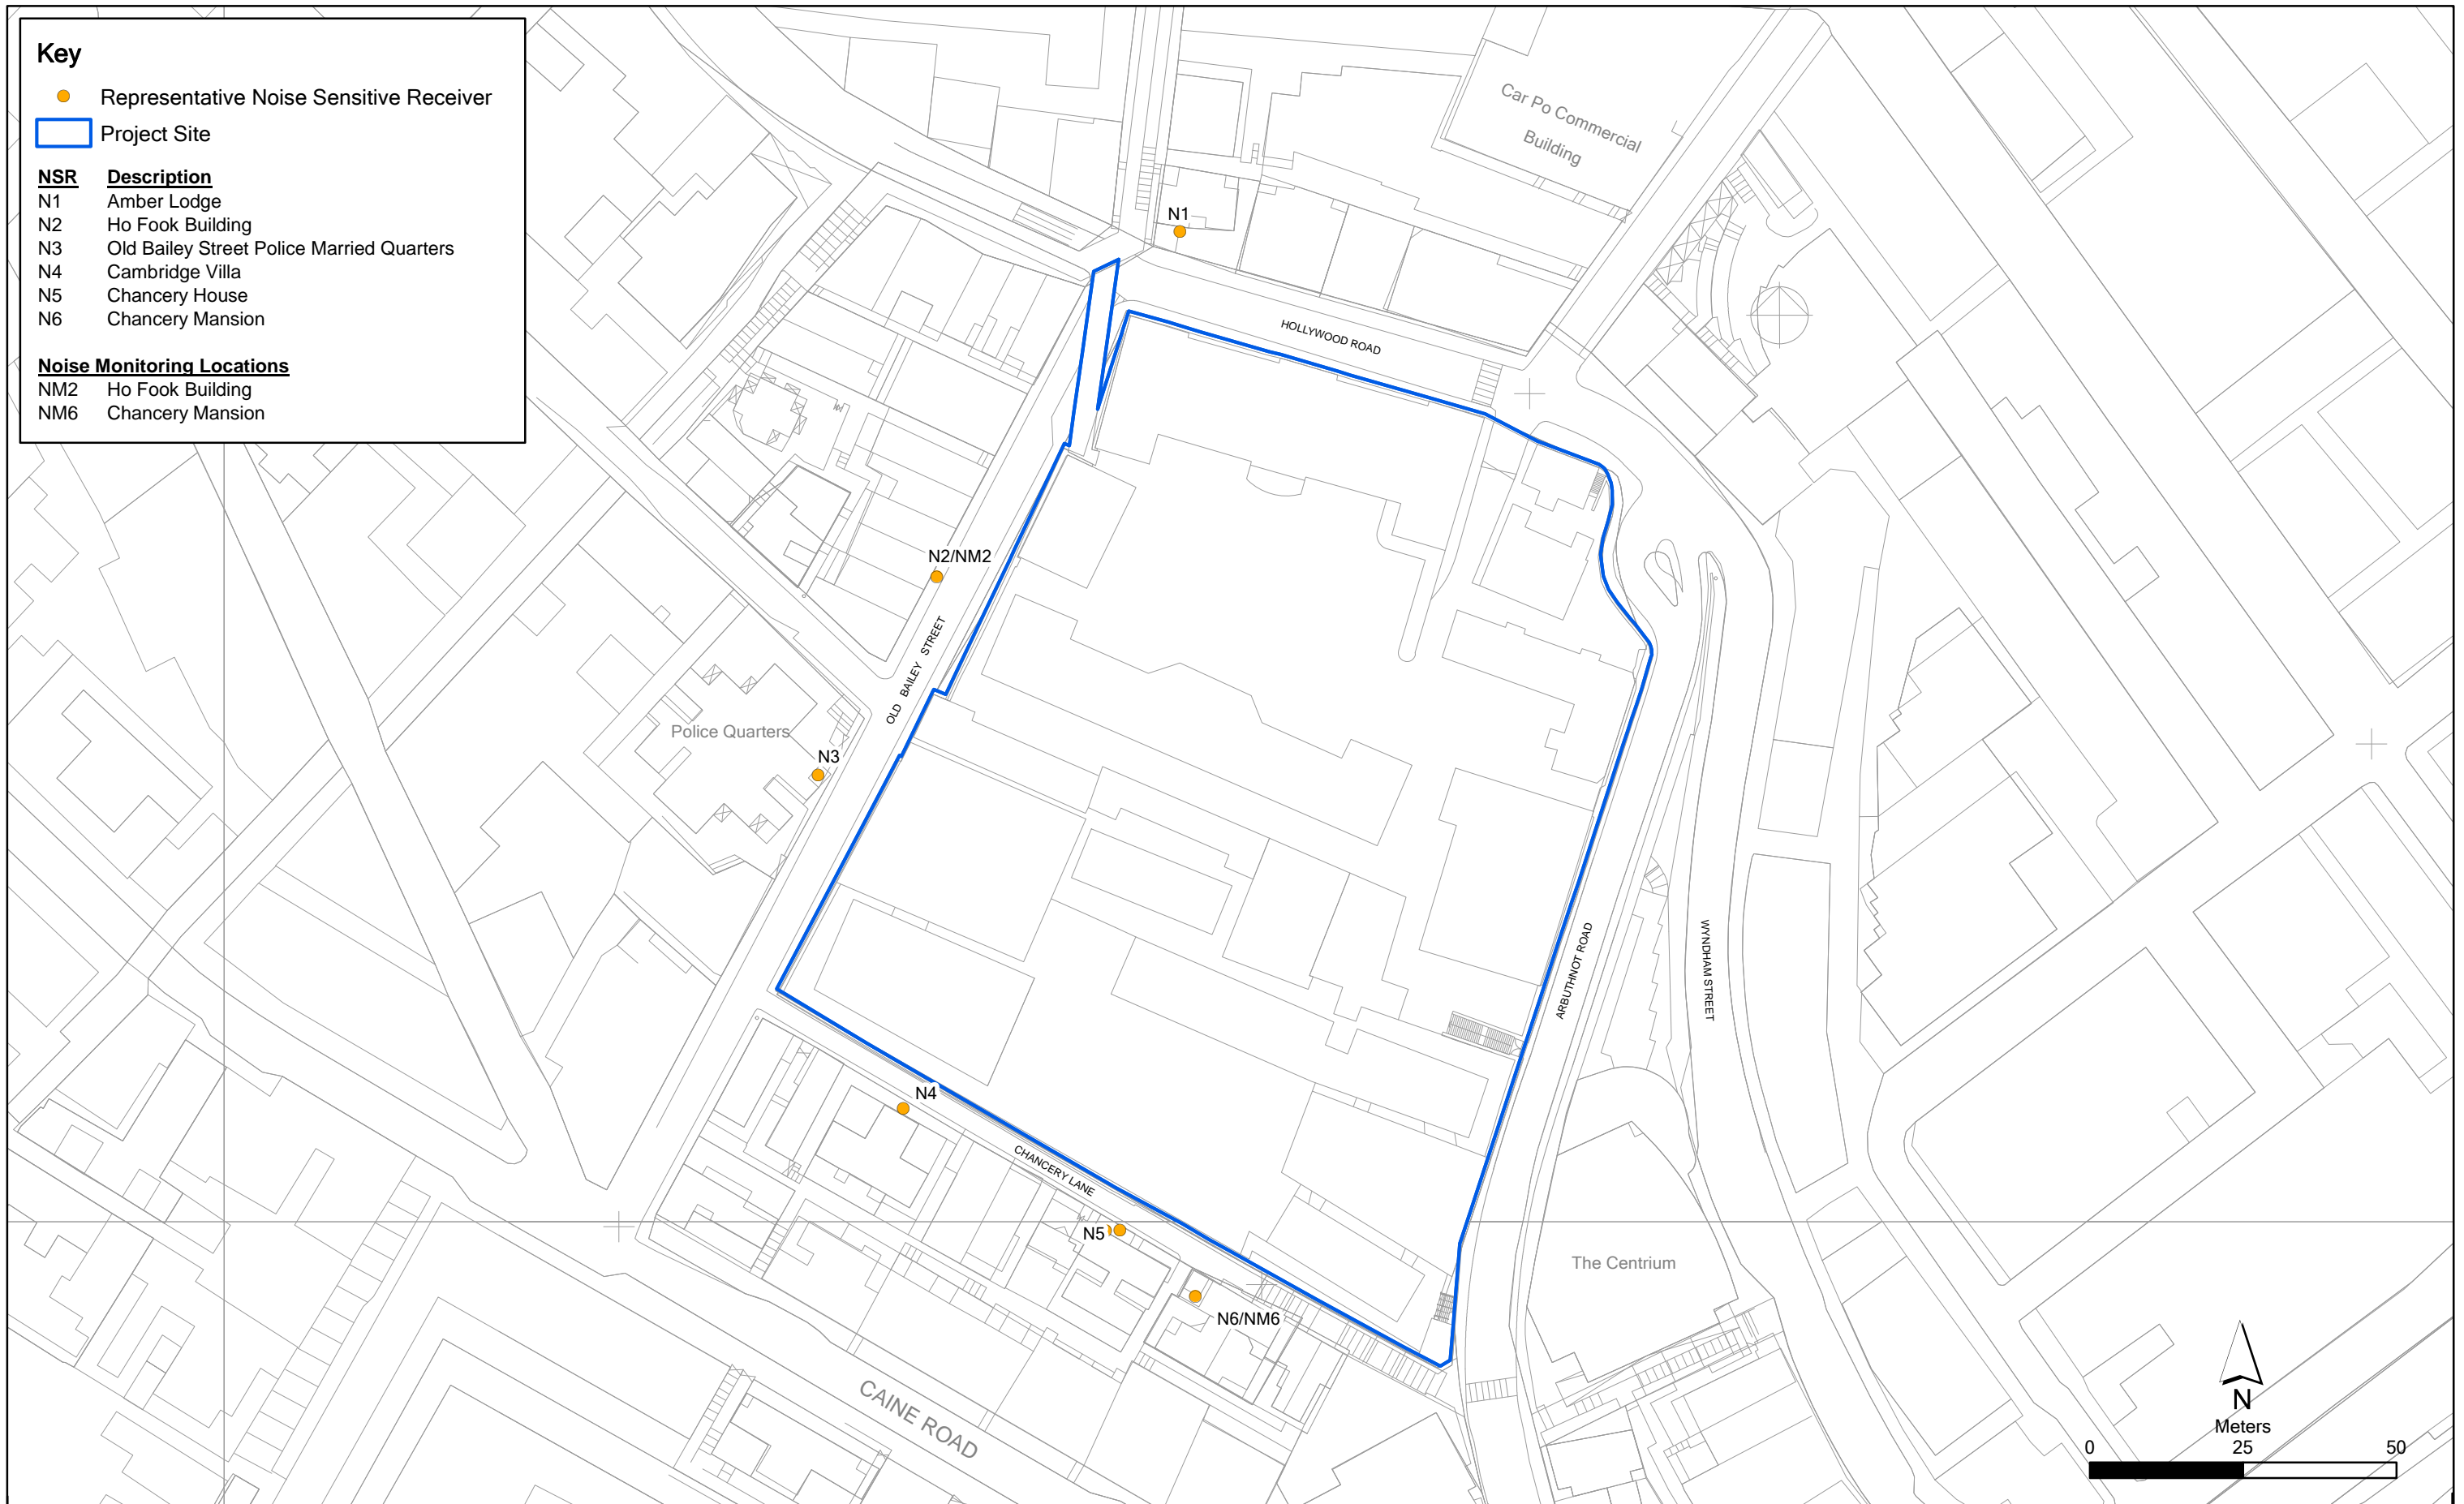

Annex C

Location of Representative Noise Sensitive Receivers and Noise Monitoring Locations

File: 0095646\_NSR\_NM\_May2012.mxd  
Date: 09/05/2012



賽馬會文物保育有限公司  
The Jockey Club CPS Limited

Annex D

## Monitoring Schedule of the Reporting Period and Next Month

**Central Police Station Compound Conservation and Revitalisation  
(Ho Fook Building - NM2 & Chancery Mansion - NM6)  
Monitoring Schedule for Next Reporting Month - November 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				01-Nov	02-Nov	03-Nov
				Noise Monitoring at NM2 & NM6		
04-Nov	05-Nov	06-Nov	07-Nov	08-Nov	09-Nov	10-Nov
			Noise Monitoring at NM2 & NM6			
11-Nov	12-Nov	13-Nov	14-Nov	15-Nov	16-Nov	17-Nov
		Noise Monitoring at NM2 & NM6				
18-Nov	19-Nov	20-Nov	21-Nov	22-Nov	23-Nov	24-Nov
	Noise Monitoring at NM2 & NM6					Noise Monitoring at NM2 & NM6
25-Nov	26-Nov	27-Nov	28-Nov	29-Nov	30-Nov	
					Noise Monitoring at NM2 & NM6	

**Central Police Station Compound Conservation and Revitalisation  
(Ho Fook Building - NM2 & Chancery Mansion - NM6)  
Monitoring Schedule for Next Reporting Month - December 2012**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						01-Dec
02-Dec	03-Dec	04-Dec	05-Dec	06-Dec	07-Dec	08-Dec
				Noise Monitoring at NM2 & NM6		
09-Dec	10-Dec	11-Dec	12-Dec	13-Dec	14-Dec	15-Dec
			Noise Monitoring at NM2 & NM6			
16-Dec	17-Dec	18-Dec	19-Dec	20-Dec	21-Dec	22-Dec
		Noise Monitoring at NM2 & NM6				
23-Dec	24-Dec	25-Dec	26-Dec	27-Dec	28-Dec	29-Dec
	Noise Monitoring at NM2 & NM6					Noise Monitoring at NM2 & NM6
30-Dec	31-Dec					

Annex E

# Calibration Reports for Calibrators and Sound Level Meters



# Certificate of Calibration

## 校正證書

Certificate No. : C124011  
證書編號

### ITEM TESTED / 送檢項目 ( Job No. / 序引編號 : IC12-1674 )

Description / 儀器名稱 : Sound Level Calibrator  
Manufacturer / 製造商 : Rion  
Model No. / 型號 : NC-73  
Serial No. / 編號 : 10997142  
Supplied By / 委託者 : Envirotech Services Co.  
Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,  
Hong Kong

### TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$       Relative Humidity / 相對濕度 :  $(55 \pm 20)\%$   
Line Voltage / 電壓 : ---

### TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 9 July 2012

### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
All results are within manufacturer's specification.  
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By :   
測試 : L K Yeung

Certified By :   
核證 : K C Lee

Date of Issue : 10 July 2012  
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C124011  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C123541
CL281	Multifunction Acoustic Calibrator	DC110233
TST150A	Measuring Amplifier	C120886

- Test procedure : MA100N.

- Results :

### 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.5	± 0.2

### 5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	0.990	1 kHz ± 2 %	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

### Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

# Certificate of Calibration

## 校正證書

Certificate No. : C124191  
證書編號

### ITEM TESTED / 送檢項目 ( Job No. / 序引編號 : IC12-1770 )

Description / 儀器名稱 : Sound Level Meter  
Manufacturer / 製造商 : Rion  
Model No. / 型號 : NL-31  
Serial No. / 編號 : 00603867  
Supplied By / 委託者 : Envirotech Services Co.  
Shop 6, G/F., Casio Mansion, 209 Shaukeiwan Road,  
Hong Kong

### TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C  
Line Voltage / 電壓 : ---  
Relative Humidity / 相對濕度 : (55 ± 20)%

### TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 18 July 2012

### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
All results are within manufacturer's specification.  
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies, USA
- Fluke Everett Service Center, USA
- Fluke Precision Measurement Ltd., UK
- Rohde & Schwarz Laboratory, Germany

Tested By :   
測試 : L K Yeung

Certified By :   
核證 : K C Lee

Date of Issue : 18 July 2012  
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C124191  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL280	40 MHz Arbitrary Waveform Generator	C120016
CL281	Multifunction Acoustic Calibrator	DC110233

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.8	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.8 (Ref.)
				104.00		103.8
				114.00		113.8

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.8	Ref.
			Slow			93.7	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C124191  
證書編號

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L <sub>A</sub>	A	Fast	94.00	63 Hz	67.6	-26.2 ± 1.5
					125 Hz	77.6	-16.1 ± 1.5
					250 Hz	85.1	-8.6 ± 1.4
					500 Hz	90.6	-3.2 ± 1.4
					1 kHz	93.8	Ref.
					2 kHz	95.1	+1.2 ± 1.6
					4 kHz	95.0	+1.0 ± 1.6
					8 kHz	92.8	-1.1 (+2.1 ; -3.1)
					12.5 kHz	89.9	-4.3 (+3.0 ; -6.0)

#### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L <sub>C</sub>	C	Fast	94.00	63 Hz	93.0	-0.8 ± 1.5
					125 Hz	93.6	-0.2 ± 1.5
					250 Hz	93.8	0.0 ± 1.4
					500 Hz	93.9	0.0 ± 1.4
					1 kHz	93.9	Ref.
					2 kHz	93.7	-0.2 ± 1.6
					4 kHz	93.2	-0.8 ± 1.6
					8 kHz	90.9	-3.0 (+2.1 ; -3.1)
					12.5 kHz	88.1	-6.2 (+3.0 ; -6.0)

Remarks : - Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz : ± 0.35 dB  
 250 Hz - 500 Hz : ± 0.30 dB  
 1 kHz : ± 0.20 dB  
 2 kHz - 4 kHz : ± 0.35 dB  
 8 kHz : ± 0.45 dB  
 12.5 kHz : ± 0.70 dB  
 104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)  
 114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

#### Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606

Fax/傳真: 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Annex F

## Event / Action Plans for Noise

*Annex F Event and Action Plan for Noise*

Event	Action			
	Environmental Team (ET)	Independent Environmental Checker (IEC)	Authorised Person (AP)	Contractor
<b>Action Level</b>	<ol style="list-style-type: none"> <li>1. Notify IEC and Contractor;</li> <li>2. Carry out investigation;</li> <li>3. Report the results of investigation to the IEC, AP and Contractor;</li> <li>4. Discuss with the Contractor and formulate remedial measures;</li> <li>5. Increase monitoring frequency to check mitigation effectiveness.</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the analysed results submitted by the ET;</li> <li>2. Review the proposed remedial measures by the Contractor and advise the AP accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to proposed remedial measures for the analysed noise problem;</li> <li>4. Ensure remedial measures are properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to IEC;</li> <li>2. Implement noise mitigation proposals.</li> </ol>
<b>Limit Level</b>	<ol style="list-style-type: none"> <li>1. Identify source;</li> <li>2. Inform IEC and AP;</li> <li>3. Repeat measurements to confirm findings;</li> <li>4. Increase monitoring frequency;</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>6. Inform IEC, AP and EPD the causes and actions taken for the exceedances;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and AP informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst AP, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the AP accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>4. Ensure remedial measures properly implemented;</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Resubmit proposals if problem still not under control;</li> <li>5. Stop the relevant portion of works as determined by the AP until the exceedance is abated.</li> </ol>

Annex G

## Summary of Implementation Status



**Annex G Implementation Schedule for Environmental Protection Measures**

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
<i>Cultural Heritage</i>					
S3.9.1	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	To be advised	During detailed design and construction	√
S3.9.2	S3.3.1	<p><u>Vibration Monitoring</u></p> <p>A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO’s prior approval before commencement of the construction works.</p>	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	√
S3.9.2	S3.3.3	<p><u>Compliance of the Approved Measures and Auditing</u></p> <p>Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures.</p> <p>Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team (“the Heritage Checker”) to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed proposal of the regular audit such as methodology (e.g. performance</p>	Whole site	Prior to and during construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement.  The Heritage Checker shall also attend the regular site meetings with AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	<u>Archival Recording</u> An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of as-built drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	<u>General Construction Methods</u> Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be checked and confirmed by the contractor. Non-percussive piling	Whole site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		<p>methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure.</p>			
S3.7.1 & 3.7.2	-	<p>Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose:</p> <ul style="list-style-type: none"> <li>• one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and</li> <li>• an updated inventory list of the historic features together with the cross referenced location plans and photo records.</li> </ul> <p>One set of updated CMP shall be submitted to the AMO for approval before the operation stage of the project.</p>	Whole site	During detailed design, construction, post-construction and operation	√ - CMP was implemented during the reporting month. There were no updates for the CMP.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
<i>Landscape &amp; Visual</i>					
S4.7.27	-	<p><u><i>In-situ Tree Protection - Cordon Zone (CZ)</i></u></p> <p>Cordon off each tree along its drip line (below the crown) with a chain-link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.</p>	Whole site	During construction	√
S4.7.2	-	<p><u><i>In-situ Tree Protection - Advanced &amp; Phased Root Pruning</i></u></p> <p>All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter &gt;20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.</p>	Whole site	During construction	N/A – no root pruning has been conducted yet
S4.7.2	-	<p><u><i>In-situ Tree Protection - Foliage cleansing system</i></u></p> <p>A sprinkler cleansing system will be installed either in the crown of the tree or at a suitable location on an adjacent building to provide the</p>	Whole site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		means to wash the foliage of the accumulated dust when necessary, particularly in the dry season.			
S4.7.2	S4	<p><u>In-situ Tree Protection - Monthly inspection</u></p> <p>Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (<a href="http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf">http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf</a>) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days.</p>	Whole site	During construction	√
S4.7.2	-	<p><u>Light Control</u></p> <p>Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.</p>	Whole site	During construction and operation	√
S4.7.2	S4	<p><u>Compensatory Tree Planting</u></p> <p>A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10. The existing tree site will be enlarged to become a wide tree strip to accommodate at least six trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth.</p> <p>The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil underneath so that fertilizers and conditioners could be added on a</p>	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	N/A – Compensatory Tree Planting will be conducted at later stage.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		<p>regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.</p> <p>Pursuant to the “Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation”, the compensation ratio should preferably be 1:1 according to trunk girth. T10 has a DBH of 20 cm (Table 4.3), and it is proposed that six trees of heavy standard size be planted, each with a DBH of around 10 cm and root balls of not less than 0.75 m diameter and 0.75 m depth,. Since the aggregate DBH of the new trees would be 60 cm, the rate of compensation is equivalent to three times the DBH of T10, far beyond the requirements</p> <p>The six replacement trees should be planted in the new tree strip in two staggered rows, maximising distance between each tree to avoid mutual interference in the future. It is recommended that the species selected should have a small final dimension of less than 10 m height given the proximity to built structures such as the retaining wall and buildings. Two each of the outstanding and related flowering tree species connected to local natural history are suggested::</p> <ul style="list-style-type: none"> <li>– <i>Bauhinia</i> ‘Blakeana’ a native evergreen species with deep mauve flowers and an exceptionally long flowering period from late autumn to early spring.</li> <li>– <i>Bauhinia purpure</i>, a native evergreen with lighter purple flowers from late autumn to early winter.</li> <li>– <i>Bauhinia variegata</i>, an exotic deciduous species, with pale pinkish flowers in spring to early summer often when the tree has little or no leaves.</li> </ul>			
S4.7.2	S4	<p><u>Vertical Greening</u></p> <p>Within the limitations of the conservation of the CPS character, greening of vertical structures should be provided where possible.</p> <p>As such it is recommended that the inner southern wall of the Site be planted as a green wall. The plantings should be inserted in between each of the large protruding piers and an offset be made from both the</p>	Inner Southern Wall	During detailed design and construction	N/A – No vertical greening was conducted during the reporting month.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		top and bottom edge so that old and new are equally visible. An independent frame should be strategically positioned in order to ensure minimal disturbance to the original wall, and provide the main structural support and planting surface for the green wall. The frame on to which the new green will be planted should contain its own irrigation system so that moisture for the plants will remain mainly on the planting surface and not the existing wall behind. The planting chosen should be appropriate to the Hong Kong climate, requiring relatively little maintenance to sustain the quality of both plants and wall.			
S4.7.2	-	<b><i>New Custom Paving</i></b>  New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	N/A – No custom paving was conducted during the reporting month.
S4.7.2	S4	<b><i>In-situ Tree Protection - Quarterly inspection</i></b>  Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau ( <a href="http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf">http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf</a> ) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction.	Whole site	During post construction and operation	N/A – The quarterly inspection will be conducted at later stage.
<i>Noise</i>					
S5.9	-	The following site practices should be followed during the construction of the Project: <ul style="list-style-type: none"> <li>• Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase;</li> <li>• Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase;</li> <li>• Mobile plant, if any, will be sited as far away from NSRs as possible;</li> </ul>	Whole Site	During construction	N/A – Not observed.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		<ul style="list-style-type: none"> <li>Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum;</li> <li>Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.</li> </ul>			
S5.9	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	√
S5.9	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m <sup>-2</sup> and have no openings or gaps.	Whole Site	During construction	√
S5.9	-	Use quiet PME as far as practicable to mitigate the construction noise impact.	Whole Site	During construction	√
S5.9	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	√
S5.11	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage.	Whole Site	During construction	√
<i>Air Quality</i>					
S6.8.1	-	Dust control measures stipulated in the <i>Air Pollution Control (Construction Dust) Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	√



EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	√
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	√
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	√
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	√
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	√
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	√
S6.8.1	-	Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	√
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	N/A – Not observed.
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if required, from the ground floor level of building for construction of superstructure of the new buildings.	Whole Site	During construction	√
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	√
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	N/A – Not observed.
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	√
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A – Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	√
<i>Water Quality</i>					
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1 of ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	√
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A – Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	√
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	√
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	√
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A – Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A – Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	√
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	√
<i>Waste Management</i>					
S8.5	S6.3.1 & Table 6.1	<u>General</u> The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	√
S8.5	-	<u>Management of Waste Disposal</u> The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid “chit” which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	√
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket system will be included as one of the contractual requirements and implemented by the contractor.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated /recycled and disposed of will be established during the construction phase.	Whole Site	During construction	√
S8.5	S6.3	<u>Reduction of Construction Waste Generation</u>  C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	√
S8.5	S6	<u>Chemical Waste</u>  The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	√
S8.5	S6	Containers used for storage of chemical waste shall: <ul style="list-style-type: none"> <li>• Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed;</li> <li>• Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and</li> <li>• Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2 of the Regulations</i>.</li> </ul>	Whole Site	During construction and operation	√
S8.5	S6	Storage areas for chemical waste shall: <ul style="list-style-type: none"> <li>• Be clearly labelled and used solely for the storage of chemical waste;</li> <li>• Be enclosed on at least 3 sides;</li> <li>• Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest;</li> <li>• Have adequate ventilation;</li> <li>• Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and</li> <li>• Be arranged so that incompatible materials are appropriately separated.</li> </ul>	Whole Site	During construction and operation	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	N/A – Not observed.
S8.5	S6 & Table 6.1	<u>General Refuse</u> General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	√
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	√
S8.5	S6	<u>Staff Training</u> At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commence-ment of construction	√
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	√

Remark:

- √ Compliance of Mitigation Measures
- <> Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd
- △ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd
- N/A Not Applicable in Reporting Period


Annex H

## Noise Monitoring Results






Normal Weekdays Noise Monitoring Results at NM6 - Chancery Mansion (Leq, 30min)

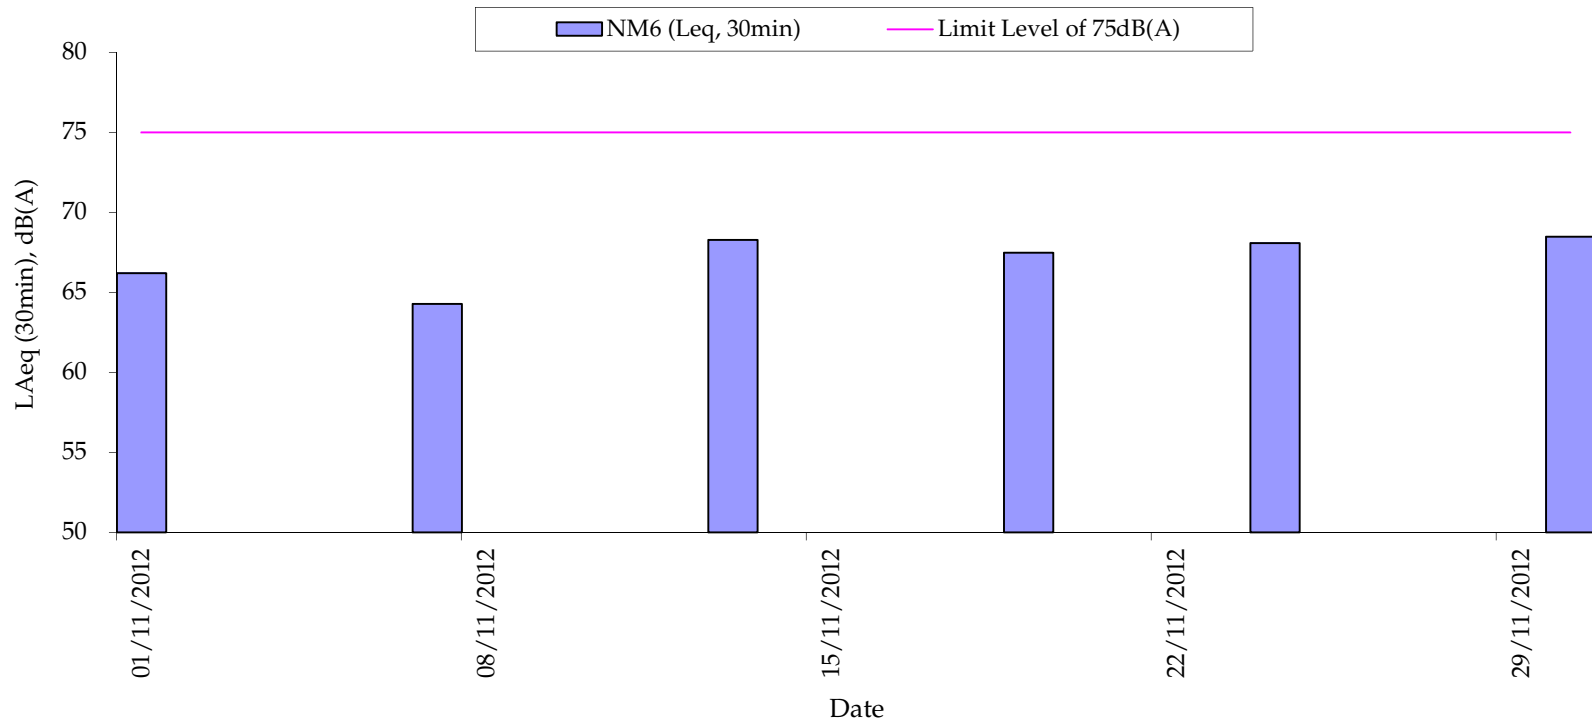

Remark:

- 75dB(A) was adopted as the Limit Level during normal weekdays in the reporting period

Normal Weekdays Noise Monitoring Results at NM2 - Ho Fook Building (Leq, 30min)

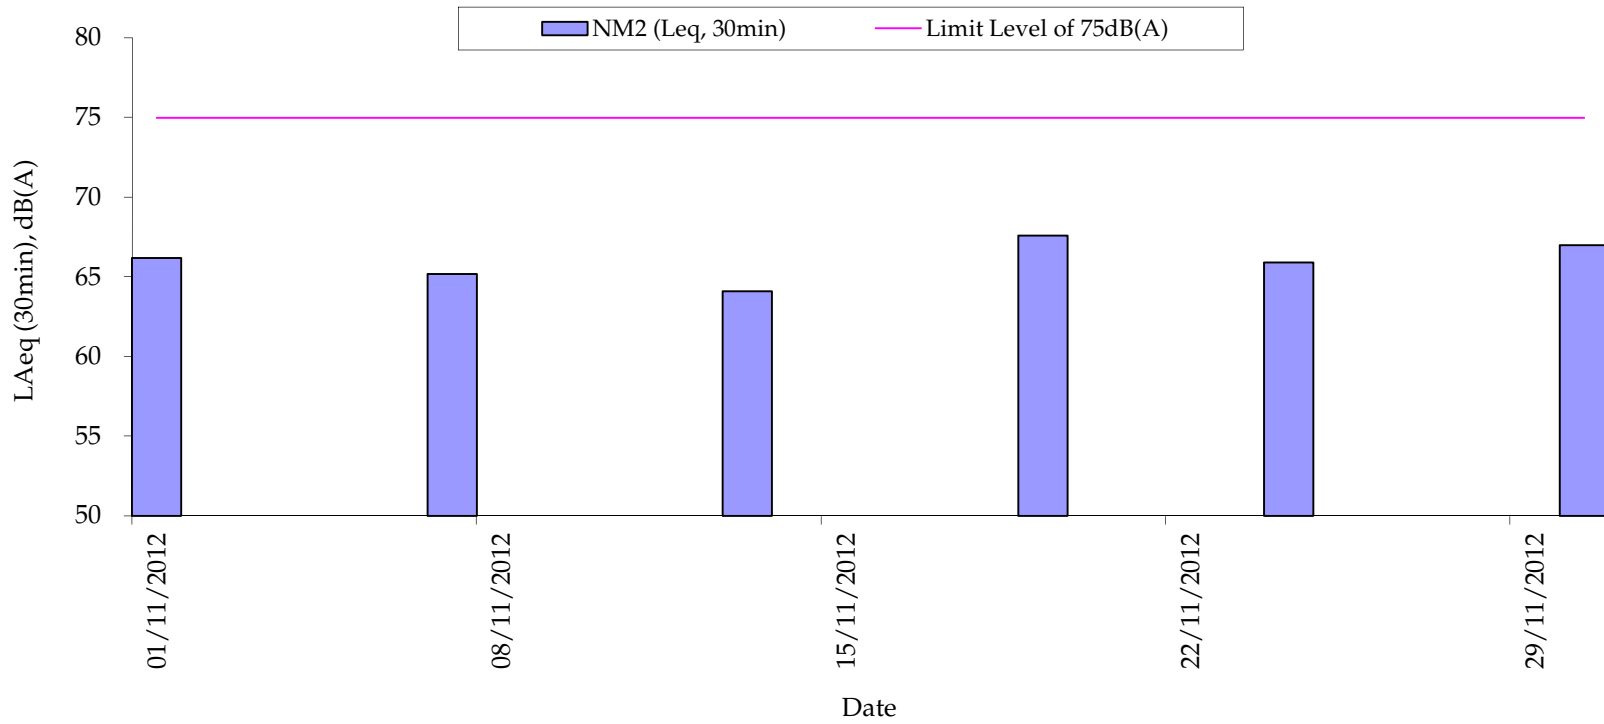

Remark:

- 75dB(A) was adopted as the Limit Level during normal weekdays in the reporting period

Annex I

# Construction Programme for the Project

Activity ID	Activity Description	Duration in Days	2011		2012				2013				2014				2015				2016																																	
			J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S
<b>GENERAL</b>																																																						
S110	PRECONSTRUCTION WORKS	592	PRECONSTRUCTION WORKS																																																			
<b>EXISTING BUILDINGS</b>																																																						
160010	BLOCK 16 WORKSHOP & LAUNDRY (DEMOLITION WORKS)	198	BLOCK 16 WORKSHOP & LAUNDRY (DEMOLITION WORKS)																																																			
180010	BLOCK 18/14 ANNEX/BLDG F/G/H/ (DEMOLITION WORKS)	149	BLOCK 18/14 ANNEX/BLDG F/G/H/ (DEMOLITION WORKS)																																																			
080010	BLOCK 08 ABLUTIONS BLOCK	731	BLOCK 08 ABLUTIONS BLOCK																																																			
170005	BLOCK 17 F HALL	593	BLOCK 17 F HALL																																																			
010005	BLOCK 01 POLICE HEADQUARTERS BLOCK	593	BLOCK 01 POLICE HEADQUARTERS BLOCK																																																			
140005	BLOCK 14 D HALL	645	BLOCK 14 D HALL																																																			
120010	BLOCK 12 B HALL	341	BLOCK 12 B HALL																																																			
110010	BLOCK 11 A HALL	311	BLOCK 11 A HALL																																																			
100010	BLOCK 10 SUPERINTENDENT'S HOUSE	484	BLOCK 10 SUPERINTENDENT'S HOUSE																																																			
130010	BLOCK 13 C HALL	484	BLOCK 13 C HALL																																																			
060005	BLOCK 06 MARRIED SERGEANTS' QUARTERS	223	BLOCK 06 MARRIED SERGEANTS' QUARTERS																																																			
070005	BLOCK 07 SINGLE INSPECTORS' QUARTERS	225	BLOCK 07 SINGLE INSPECTORS' QUARTERS																																																			
030005	BLOCK 03 BARRACK BLOCK	440	BLOCK 03 BARRACK BLOCK																																																			
020005	BLOCK 02 ARMOURY	392	BLOCK 02 ARMOURY																																																			
090005	BLOCK 09 CENTRAL MAGISTRACY	392	BLOCK 09 CENTRAL MAGISTRACY																																																			
150010	BLOCK 15 E HALL	304	BLOCK 15 E HALL																																																			
040005	BLOCK 04 MARRIED INSPECTORS' QUARTERS	349	BLOCK 04 MARRIED INSPECTORS' QUARTERS																																																			
190005	BLOCK 19 BAUHINIA HOUSE	277	BLOCK 19 BAUHINIA HOUSE																																																			
050002	BLOCK 05 (DEMOLITION WORKS)	119	BLOCK 05 (DEMOLITION WORKS)																																																			
<b>OTHER WORKS</b>																																																						
253110	REVTMENT WALL / U/G UTILITIES / ROAD WORKS	679	REVTMENT WALL / U/G UTILITIES / ROAD WORKS																																																			
<b>NEW BUILDINGS</b>																																																						
S200	OBW OLD BAILEY WING	1,097	OBW OLD BAILEY WING																																																			
S300	AW ARBUTHNOT WING	1,056	AW ARBUTHNOT WING																																																			
<b>BASEMENT PLANTROOM AND SERVICES TRENCH</b>																																																						
202005	BASEMENT PLANTROOM / SERVICES TRENCH	588	BASEMENT PLANTROOM / SERVICES TRENCH																																																			
<b>NEW FOOTBRIDGE</b>																																																						
2300125	PROPOSED FOOTBRIDGE	699	PROPOSED FOOTBRIDGE																																																			



T76G

**CENTRAL POLICE STATION CONSERVATION AND REVITALIZATION  
(MANAGEMENT CONTRACT)  
CONSTRUCTION PROGRAMME  
SUMMARY PROGRAMME**

Sheet 1 of 1

Date		Revision		Checked	Approved
13NOV12	for EPD				

GCL / P / J3416 /SUM/CP01

Annex J

## Tree Inspection Reports



欣榮 (香港) 環境管理有限公司

Yan Wing (Hong Kong) Environment Management Limited

香港 新界 沙頭角 新樓街 15 號 二樓  
No. 15, San Lau Street, 1/F., Sha Tau Kok, N.T., Hong Kong

通信地址 (Mail Address) : 上水郵局信箱 八八九 號 (Sheung Shui Post Office Box 889)

Tel: 9776 1987, 2486 2317 Fax: 2482 4667 E-mail: yanwinghk@netvigator.com

R03595

RECEIVED  
30 NOV 2012

15<sup>th</sup> November 2012

Our Ref. : YW/TP/GAMMON/2012/11/2

Gammon Construction Limited  
28/F Devon House  
TaiKoo Place 979 King's Road  
Hong Kong  
Attn : Mr. Cliff C.H. LEUNG

Tel. 2516 8823  
Fax.2516 6260

Dear Sir,

**Summary of Monthly Inspection Report for the Six Existing Trees  
at Central Police Station Compound for November 2012  
( Contract Ref. : J3416/400.4/D00025 )**

Tree No.	Botanical Name	Date of Inspection	Overall Health Condition Good/Fair/Poor	Remarks
Tree-5	<i>Mangifera indica</i> 芒果	1 <sup>st</sup> Nov. 2012	Good	N.F.A.
Tree-6	<i>Aleurites moluccana</i> 石栗	1 <sup>st</sup> Nov. 2012	Fair	1.To inspect the cracks weekly.
Tree-7	<i>Aleurites moluccana</i> 石栗	1 <sup>st</sup> Nov. 2012	Fair	1.To inspect the cracks weekly.
Tree-8	<i>Plumeria rubra</i> 紅雞蛋花	1 <sup>st</sup> Nov. 2012	Fair	N.F.A.
Tree-9	<i>Araucaria cunninghamia</i> 花旗杉	1 <sup>st</sup> Nov. 2012	Fair	N.F.A.
Tree-11	<i>Dracaena marginata</i> 馬尾鐵	1 <sup>st</sup> Nov. 2012	Fair	1.To keep the wooden door always closed.



**FORM 1: TREE GROUP INSPECTION FORM**

**表格 1: 樹群檢查表格**

**General Information 基本資料**

Company 公司:	<b>Gammon Construction Ltd</b>	Name of Tree Inspection officer 巡查人員姓名:	<b>HO Kun Chung</b>
File Ref. 檔案編號:	<b>YW/TP/GAMMON/2012/11/3</b>	Name of Endorsement Officer 覆核人員姓名:	<b>WONG Pak Hay</b>
Date of Inspection 巡查日期:	<b>November 1, 2012</b>		
Project/Contract No. 合約/工程編號:	<b>J3416/400.4/D00025</b>		

**Location Information 位置資料**

Location 地點:	<b>Central Police Station Compound</b>	Nearby Utility Post No. 就近公用設施編號:	
Location Types 地點類別: Address: __ (multiple answers allowed) 可選多於一項	<input type="checkbox"/> Roadside 路旁 <input checked="" type="checkbox"/> Open space 空地 <input type="checkbox"/> Exhibition Centre 展覽中心 <input type="checkbox"/> View Point 觀景台 <input type="checkbox"/> Walking / nature trail 行山徑 / 自然徑 <input type="checkbox"/> Others (please specify) 其他 (請說明): _____		
	<input type="checkbox"/> Community Hall / Centre 社區會堂 / 中心 <input type="checkbox"/> Roadside Planter 路旁花園 <input type="checkbox"/> Rain shelter / pavilion 避雨亭 / 涼亭 <input type="checkbox"/> Sitting out area 休憩處		

**General Tree Information 基本樹木資料**

\* Delete as appropriate 請把不合適的刪除

Main tree species in the group or minority tree species of significant size 在群組內的主要樹種或樹幹胸徑或高度或樹冠範圍較大的樹種 (Note 2)	Approx. number of trees in the relevant species or as a % of tree group 該樹種在群組內的百分比/數目*	Range of tree height (m) 該樹種高度範圍	Overall health condition 整體健康狀況 (good, fair, poor 好, 良, 差)	Overall structural condition 整體結構狀況 (good, fair, poor 好, 良, 差)	Other remarks (Any special tree condition, e.g. dying/dead, pest/disease problem and structural defects; and soil condition 其他評語 (樹木狀況例如: 凋謝/枯樹/病蟲害或結構問題; 及泥土狀況)
<i>Mangifera indica</i> 芒果	17%, 1 No.	16M	GOOD	GOOD	N.F.A.
<i>Aleurites moluccana</i> 石栗	32% 2 Nos.	10-13M	FAIR	FAIR	1. To inspect the cracks weekly. 2. To remove the drooping branches/leaves of Tree-7
<i>Plumeria rubra</i> 紅雞蛋花	17% 1 No.	7M	FAIR	FAIR	N.F.A.
<i>Araucaria cunninghamia</i> 花旗杉	17% 1 No.	13M	FAIR	FAIR	N.F.A.
<i>Dracaena marginata</i> 馬尾鐵	17% 1 No.	8M	FAIR	FAIR	1. To keep the wooden door always closed.

**Target 目標**

<b>TARGET</b> (people or property potentially affected by tree/branch failure) 目標 (因樹木倒塌或枝條斷裂而受影響的人或財產)
Does target exist? 目標是否存在? <input checked="" type="checkbox"/> Yes 是 <input type="checkbox"/> No 否
Can target be moved? 能否移除目標? <input type="checkbox"/> Yes 是 <input checked="" type="checkbox"/> No 否
Can the use of site be restricted? 可否限制場地的使用? <input checked="" type="checkbox"/> Yes 是 <input type="checkbox"/> No 否
Frequency of use of location 使用該地點的頻密程度: <input type="checkbox"/> Occasional use 偶爾使用 <input type="checkbox"/> Intermittent use 間歇使用 <input checked="" type="checkbox"/> Frequent use 經常使用 <input type="checkbox"/> Constant use 恆常使用

**Identification of Trees for Remedial Action or Detailed Tree Risk Assessment**

識別下述樹木, 以便採取風險緩減措施或進行詳細樹木風險評估

Trees falling under the following criteria 樹木屬於以下任何一項或多於一項類別	Number of trees 樹木數量	Remedial action or detailed tree risk assessment 緩減措施或進行詳細樹木風險評估
(1) Trees on complaint list with structural or health problems 投訴個案中, 結構或健康問題的樹木 (Note 1)	<b>NII</b>	
(2) Mature trees belonging to species with brittle wood structure and having unsatisfactory health or structural conditions with failure potential 屬木質脆弱品種並已達成熟期及有倒塌風險的樹木 (Note 1)	<b>NII</b>	
(3) Tree with major defects or health problems 有明顯缺陷或健康問題的樹木 (Note 1)	<b>NII</b>	
(4) Trees growing in very stressful site conditions with failure potential 生長於非常擠壓環境而有倒塌風險的樹木 (Note 1)	<b>NII</b>	

**Attached Information 附夾資料**

<input type="checkbox"/> Site plan 場地平面圖 <input checked="" type="checkbox"/> Photo record 相片紀錄 <input type="checkbox"/> Others 其他 (please specify 請說明): <b>Monthly Inspection Reports</b>
---

Signature of Tree Inspection Officer: \_\_\_\_\_

Signature of Endorsement Officer: \_\_\_\_\_

Name of Contractor

**Yan Wing (HK) Environment Management Ltd.**

Date:

**15-11-2012**



Note 1: If remedial action (such as pruning) undertaken cannot mitigate the potential risk of tree or branch failure, detailed tree risk assessment (using Form 2) should be carried out

備註 1: 若風險緩減措施(如枝幹修剪)仍未解決倒塌或枝條斷裂的潛在風險, 應為該樹進行詳細的樹木風險評估(表格 2)。

Note 2: Please read in conjunction with TMO's Guidelines on Tree Risk Assessment and Management Arrangement (Para. 4.3. refers)

備註 2: 請參閱樹木管理辦事處的樹木風險評估安排及管理指引(第 4.3 節)

**Inspection Report for the 6 Existing Trees  
at Central Police Station Compound  
( Contract Ref. : J3416/400.4/D00025 )**

I. TREE NUMBER : Tree-5 *Mangifera indica* 芒果

II. BASIC INFORMATION :

Height (m)	16m	Crown spread (m)	18m
DBH (mm)	1000mm	Overall Health Condition Good/Fair/Poor	Good
Date of Inspection	1 <sup>st</sup> November 2012	Last Inspection Date	9 <sup>th</sup> October 2012

III. COMMENTS :

1. Overall health condition of the tree is good.
2. Cleanliness of the planter is acceptable.
3. The site inside the cordon zone is clean and tidy.
4. Appropriate notice displays in front of the cordon zone.
5. Some mango fruits appear on the tree.

IV. RECOMMENDATIONS :

1. No further action is required.

V. PHOTO RECORD :

Fig 1. Tree number





Fig 2. Cleanliness of the planter is acceptable.



Fig 3 The site is clean and tidy at the time of inspection.



Fig. 4 Two pipes lead water to tree top for irrigation.



Fig. 5 Appropriate notices display in front of the cordon zone.



Fig. 6 The site outside the cordon zone is clean and tidy.



Fig. 7 Some fresh mango fruits appear on the tree.



Fig. 8 Overall view of Tree-5 during inspection on 1<sup>st</sup> November 2012.



Signature of Inspection Officer :  
(Mr. HO Kun-chung, ISA CA-HK0452A)

Signature of Endorsement Officer :  
(Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Yan Wing (HK) Environment  
Management Ltd.



Dated this :

15<sup>th</sup> November 2012.

**Inspection Report for the 6 Existing Trees  
at Central Police Station Compound  
( Contract Ref. : J3416/400.4/D00025 )**

I. TREE NUMBER : Tree-6 *Aleurites moluccana* 石栗

II. BASIC INFORMATION :

Height (m)	10m	Crown spread (m)	10m
DBH (mm)	510mm	Overall Health Condition Good/Fair/Poor	Fair
Date of Inspection	1 <sup>st</sup> November 2012	Last Inspection Date	9 <sup>th</sup> October 2012

III. COMMENTS :

1. Overall health condition of the tree is fair.
2. Quantity of the bulky item has lightly reduced at the time of inspection.
3. Cleanliness of the planter is acceptable. No new cracks have been detected.
4. Drooping branches/leaves have been removed on 1.11.2012.
5. Decayed branches have been removed from the tree top.

IV. RECOMMENDATIONS :

1. To inspect the cracks weekly.

V. PHOTO RECORD :

Fig 1. Tree number



Fig 2. Cleanliness of the planter is acceptable. No new cracks have been detected on 1.11.2012.



Fig. 3 The site appears clean and tidy during inspection on 1.11.2012.



Fig. 4 Many drooping branches/leaves appeared on the tree on 9.10.2012.



Fig. 5 Drooping branches/leaves have been trimmed on 1.11.2012.



Fig. 6 Decayed branches were found on the tree top on 9.10.2012.



Fig. 7 Decayed branches have been removed on 1.11.2012.





Fig. 8 Lots of bulky item were placed in the vicinity of the tree on 9.10.2012.



Fig. 9 Quantity of the bulky item has lightly reduced on 1.11.2012.



Fig. 10 Construction works in progress outside the cordon zone.



Fig. 11 Overall view of Tree-6 during inspection on 1.11.2012.



Signature of Inspection Officer :  
(Mr. HO Kun-chung, ISA CA-HK0452A)

Signature of Endorsement Officer :  
(Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Dated this :

  
\_\_\_\_\_  
  
\_\_\_\_\_  
Yan Wing (HK) Environment  
Management Ltd.  
\_\_\_\_\_  
15<sup>th</sup> November 2012



**Inspection Report for the 6 Existing Trees  
at Central Police Station Compound  
( Contract Ref. : J3416/400.4/D00025 )**

I. TREE NUMBER : Tree-7 *Aleurites moluccana* 石栗

II. BASIC INFORMATION :

Height (m)	13m	Crown spread (m)	12m
DBH (mm)	650mm	Overall Health Condition Good/Fair/Poor	Fair
Date of Inspection	1 <sup>st</sup> November 2012	Last Inspection Date	9 <sup>th</sup> October 2012

III. COMMENTS :

1. Overall health condition of the tree is fair.
2. Cleanliness of the planter is acceptable. No new cracks have been detected at the site.
3. The broken water-pipe has been repaired prior to inspection.
4. Some drooping branches/leaves still appear on the tree.
5. Quantity of the bulky item has lightly reduced at the time of inspection..

IV. RECOMMENDATIONS :

1. To inspect the cracks weekly.
2. To remove the drooping branches/leave from the tree.

V. PHOTO RECORD :



Fig 2. Cleanliness of the planter is acceptable.



Fig 3 The cracks in question are well-repaired. No more new cracks have been found at the time of inspection.



Fig. 4 The broken water pipe has been repaired prior to inspection.



Fig. 5 Some drooping branches/leaves still appear on the tree. Removal of such branches/leaves are recommended.

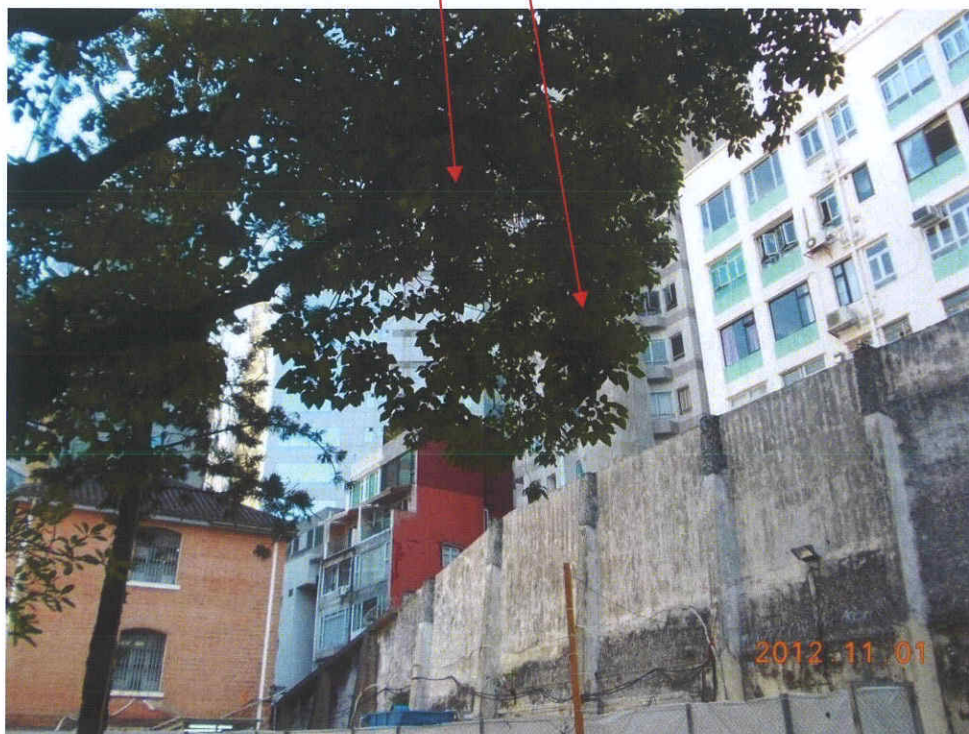


Fig. 6 Many bulky items were placed near Tree-7 on 9.10.2012.



Fig. 7 Quantity of the bulky item has lightly reduced on 1.11.2012.



Fig. 8

Overall view of Tree-7 during inspection on  
1<sup>st</sup> November 2012.



Signature of Inspection Officer :  
(Mr. HO Kun-chung, ISA CA-HK0452A)

Signature of Endorsement Officer :  
(Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Dated this :

Yan Wing (HK) Environment  
Management Ltd.

15<sup>th</sup> November 2012



**Inspection Report for the 6 Existing Trees  
at Central Police Station Compound  
( Contract Ref. : J3416/400.4/D00025 )**

I. TREE NUMBER : Tree-8 *Plumeria rubra* 紅雞蛋花

II. BASIC INFORMATION :

Height (m)	7m	Crown spread (m)	9m
DBH (mm)	430mm	Overall Health Condition Good/Fair/Poor	Fair
Date of Inspection	1 <sup>st</sup> November 2012	Last Inspection Date	9 <sup>th</sup> October 2012

III. COMMENTS :

1. Overall health condition of the tree is fair.
2. The planter is clean and tidy.
3. Cleanliness of the site is acceptable.
4. Leaves of the tree have obviously reduced.
5. The site outside the cordon zone is clean and tidy.

IV. RECOMMENDATIONS :

1. No further action is required.

V. PHOTO RECORD :

Fig 1. Tree number





Fig 2. The planter is clean and tidy.



Fig 3 Cleanliness of the site is acceptable.



Fig. 4 As dry season is drawing near, leaves of Tree-8 have obviously reduced at the time of inspection.



Fig. 5 The site outside the cordon zone is clean and tidy.



Fig. 6 Overall view of Tree-8 during inspection on 1<sup>st</sup> November 2012.



Signature of Inspection Officer :  
(Mr. HO Kun-chung, ISA CA-HK0452A)

Signature of Endorsement Officer :  
(Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Dated this :

  
\_\_\_\_\_  
Yan Wing (HK) Environment  
Management Ltd.  
\_\_\_\_\_  
15<sup>th</sup> November 2012  
\_\_\_\_\_



**Inspection Report for the 6 Existing Trees  
at Central Police Station Compound  
( Contract Ref. : J3416/400.4/D00025 )**

I. TREE NUMBER : Tree - 9 *Araucaria cunninghamia* 花旗杉

II. BASIC INFORMATION :

Height (m)	13m	Crown spread (m)	5m
DBH (mm)	230mm	Overall Health Condition Good/Fair/Poor	Fair
Date of Inspection	1 <sup>st</sup> November 2012	Last Inspection Date	9 <sup>th</sup> October 2012

III. COMMENTS :

1. Overall health condition of the tree is fair.
2. Cleanliness of the planter is acceptable.
3. The site inside the cordon zone is clean and tidy.
4. Young leaves are growing vigorous and healthy on the tree.
5. The site outside the cordon zone is clean and tidy.

IV. RECOMMENDATIONS :

1. No further action is required.

V. PHOTO RECORD :

Fig 1. Tree number



Fig 2. Cleanliness of the planter is acceptable.



Fig. 3 The site inside the cordon zone is clean and tidy.




Fig. 4 Young leaves are growing vigorous and healthy on the tree.



Fig. 5 The site outside the cordon zone is clean and tidy.



Fig. 6 Overall view of Tree-9 during inspection on 1<sup>st</sup> November 2012.

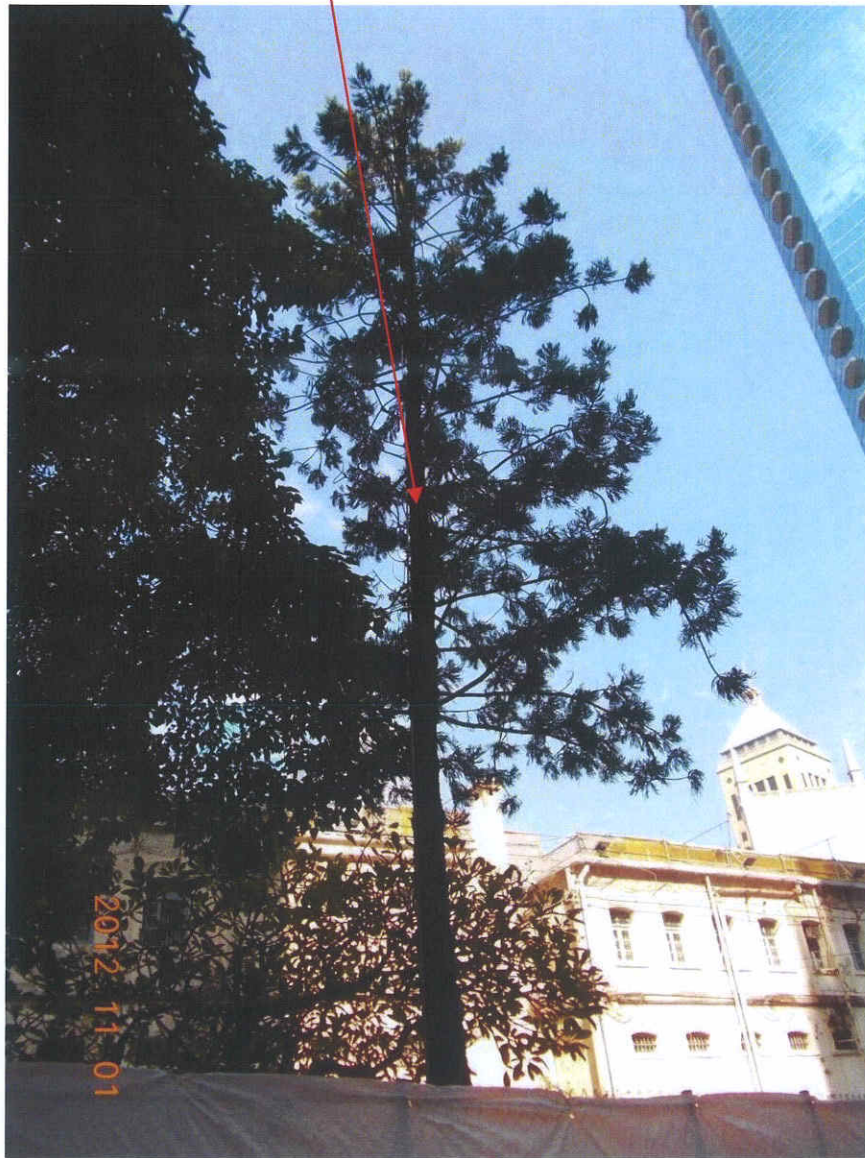

Signature of Inspection Officer :  
(Mr. HO Kun-chung, ISA CA-HK0452A)

Signature of Endorsement Officer :  
(Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Dated this :

  
\_\_\_\_\_  
  
\_\_\_\_\_  
Yan Wing (HK) Environment  
Management Ltd.  
\_\_\_\_\_  
  
\_\_\_\_\_  
15<sup>th</sup> November 2012  
\_\_\_\_\_



**Inspection Report for the 6 Existing Trees  
at Central Police Station Compound  
( Contract Ref. : J3416/400.4/D00025 )**

I. TREE NUMBER : Tree -11 *Dracaena marginata* 馬尾鐵

II. BASIC INFORMATION :

Height (m)	8m	Crown spread (m)	2m
DBH (mm)	170mm	Overall Health Condition Good/Fair/Poor	Fair
Date of Inspection	1 <sup>st</sup> November 2012	Last Inspection Date	9 <sup>th</sup> October 2012

III. COMMENTS :

1. Overall health condition of the tree is fair.
2. Cleanliness of the planter is acceptable.
3. Cleanliness of the site is acceptable.
4. The site outside the cordon zone is clean and tidy.
5. The wooden door of the building keeps opened at the time of inspection.

IV. RECOMMENDATIONS :

1. To keep the wooden door always closed.

V. PHOTO RECORD :

Fig 1. Tree number





Fig. 2 Cleanliness of the planter is acceptable.



Fig. 3 Cleanliness of the site is acceptable.



Fig. 4 The wooden door keeps opened at the time of inspection.



Fig. 5 The site outside the cordon zone is clean and tidy.



Fig. 6 Overall view of Tree-11 during inspection on 1<sup>st</sup> November 2012.



Signature of Inspection Officer :  
(Mr. HO Kun-chung, ISA CA-HK0452A)

Signature of Endorsement Officer :  
(Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Dated this :

  
\_\_\_\_\_  
  
\_\_\_\_\_  
Yan Wing (HK) Environment  
Management Ltd.  
\_\_\_\_\_  
15<sup>th</sup> November 2012  
\_\_\_\_\_



Annex K

Environmental Complaint,  
Environmental Summon  
and Prosecution Log

*Annex K Cumulative Complaint and Summons/Prosecutions Log*

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
November 2011	0	0
December 2011	0	0
January 2012	0	0
February 2012	0	0
March 2012	4	0
April 2012	0	0
May 2012	0	0
June 2012	2	0
July 2012	1	0
August 2012	0	0
September 2012	0	0
October 2012	0	0
November 2012	2	0
Overall Total	9	0

## COMPLAINT INVESTIGATION REPORT

### *Basic Information of Complaint*

Log Number:	2012/11/001
Date of Complaint Received	15 November 2012
Location of Complaint	Project Site
Nature of Complaint	Noise nuisance
Complaint Received by	Gammon Construction Limited (GCL)
Complainant	

### *Details of Complaint*

GCL has received a complaint on noise nuisance at 10:10am on 15 November 2012. The complainant, a resident living along Old Bailey street, mentioned that noise was generated from the construction site at around 7:30am for a duration of about 15 minutes. The complainant also indicated that this has been occurring for the past few months.

## Investigation Report

1. According to the information provided by the Contractor, relocation of piling machine, which was done as a preparation for the subsequent pipe piling works, was carried out near Block 8 at 7:30am on 15 November 2012. Other major construction activities undertaken on 15 November 2012 included slab demolition works at Block 8 and grouting works at Block 17, both commenced at around 9:00am.
2. The locations of the work areas are presented in Figure 1.

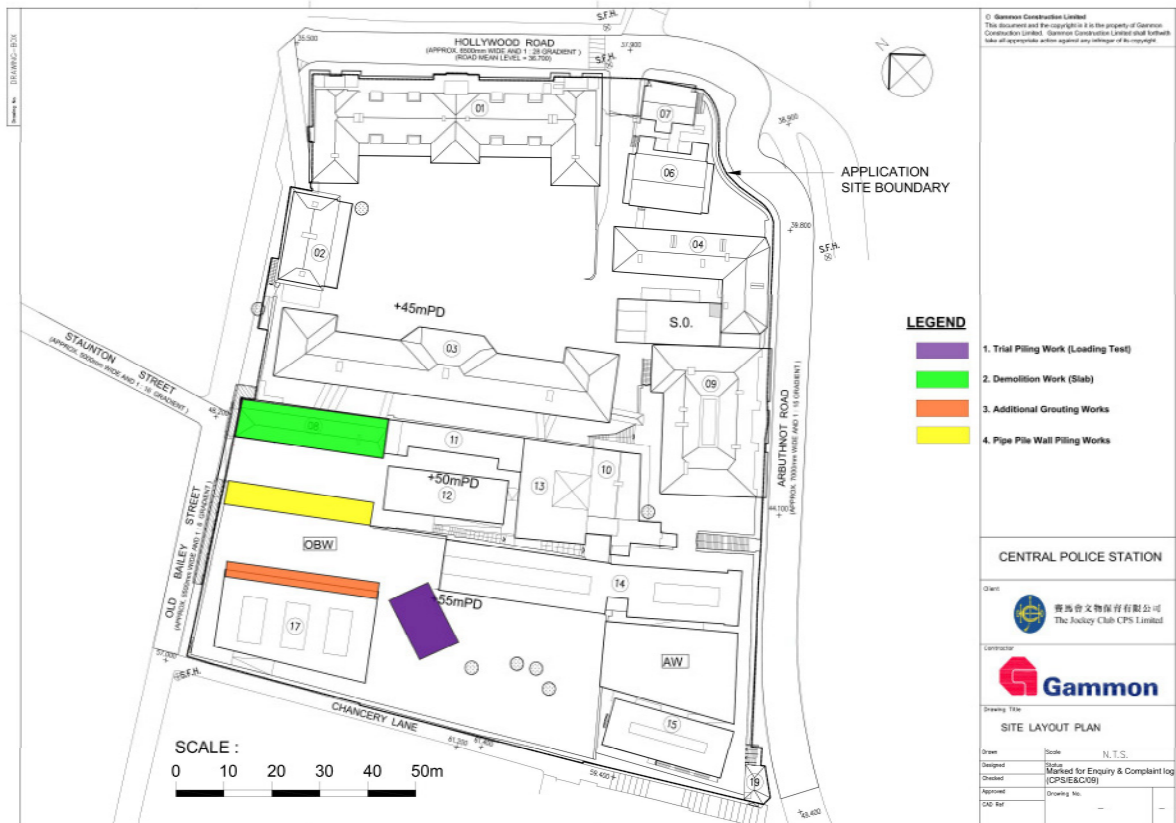


Figure 1. Locations of works being carried out on 15 November 2012

3. The noise nuisance indicated by the complainant was likely caused by the relocation of piling machine on the inclined steel platform near Block 8 at 7:30am. Friction between the track of the piling machine and the inclined steel platform as a result of the piling machine relocation could potentially generate considerable noise, which may affect residents living along the Old Bailey Street. As reported by the Contractor, acoustic curtain has been installed on the hoarding during the relocation of the piling machine. To avoid potential noise nuisance in the future, follow-up actions are proposed.

**Mitigation Measures and Follow-up Actions Recommended to Contractor**

The Contractor should follow all relevant noise requirements specified in EIA, EM&A Manual, EMP, Method Statements, General and Particular Specifications of this Project. It has been agreed with the Contractor that the relocation of piling machine will be carried out, as far as possible, at the end of the working day instead of during early morning time. The Contractor has been reminded to ensure that acoustic curtains are properly installed prior to conducting the piling machine relocation. Additionally, the Contractor has been advised to notify all workers and operation supervisor of the complaint dated 15 November 2012 and to remind them to minimise the potential noise generated as far as possible during the relocation of piling machine as well as other work activities.

Date of File Closed : 20 November 2012


Approved by:

ET Leader

IEC

JCCPS's  
Representative


Rocco Design  
Architect's  
Representative



(Name: Winnie Ko)  
Date: 20 November 2012



(Name: Sharifah Or)  
Date: 22 November 2012



(Name: C W Shau)  
Date: 13 Dec 2012



(Name: CHARLES KUNG)  
Date: 23 Nov 2012

Gammon's  
Representative



(Name: Cliff Leung)  
Date: 2012-11-20



**COMPLAINT INVESTIGATION REPORT**

*Basic Information of Complaint*


Log Number:	2012/11/002
Date of Complaint Received	23 November 2012
Location of Complaint	Project Site
Nature of Complaint	Nuisance from operating machinery emissions
Complaint Received by	Environmental Protection Department (EPD)
Complainant	

*Details of Complaint*

EPD has received a complaint on nuisance from operating machinery emissions on 23 November 2012. The complainant, a resident living along Chancery Lane, mentioned that diesel smell were perceived at his location and suspected that the emissions were originated from the construction site. The complaint was transferred to Gammon Construction Limited (GCL) on 23 November 2012 at around 16:30.

## Investigation Report

- According to the information provided by GCL, the diesel exhaust emissions may be generated by the following operating plant and/or work activities carried out in the vicinity of Chancery Lane on 23 November 2012:
  - Three operating air compressors near Block 14;
  - An operating mobile crane near Block 17; and
  - Grouting works were being conducted at the north elevation of Block 17 and three drilling machines were being operated concurrently.
- The locations of the plant/work activities are presented in *Figure 1*.

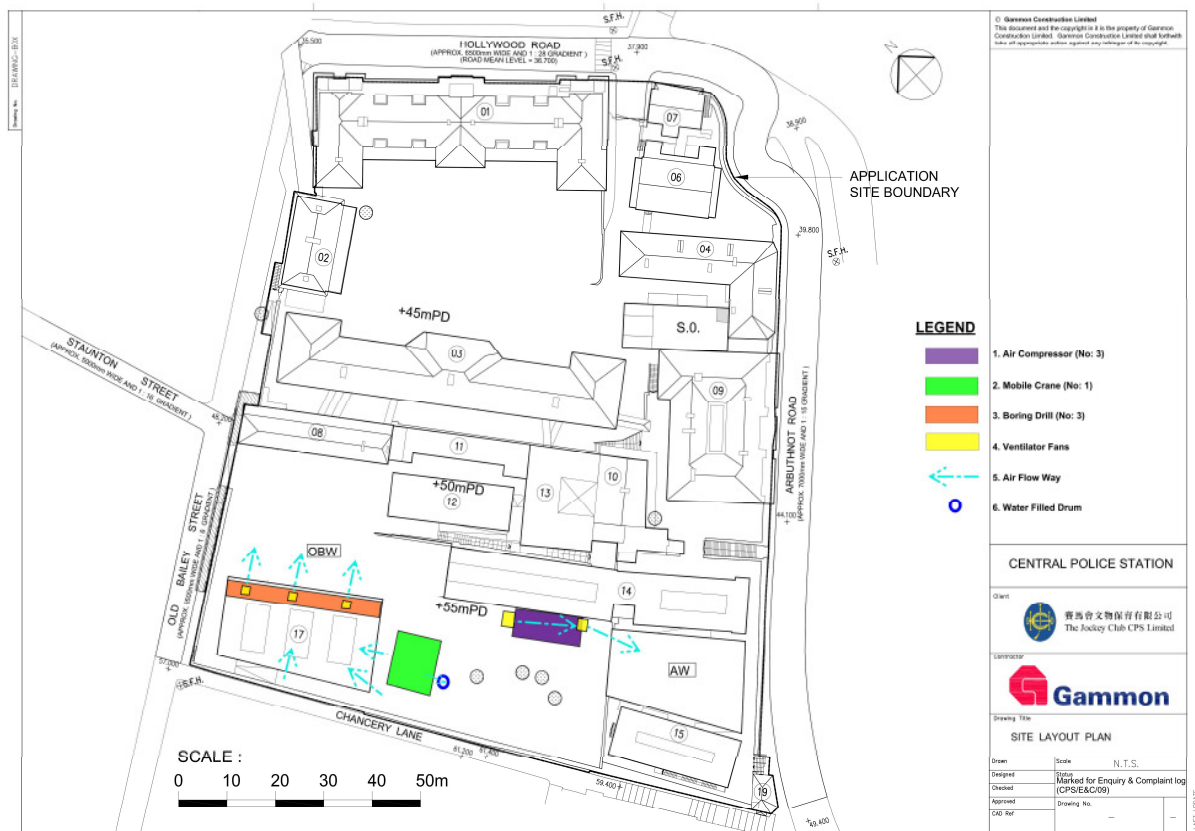

**Figure 1. Locations of plant being operated on 23 November 2012 and subsequently implemented mitigation measures for potential diesel exhaust emissions**

- The emission nuisance perceived by the complainant living along Chancery Lane may potentially be originated from the plant being operated close to Chancery Lane on 23 November 2012, as listed above. Exhaust emissions from these diesel-powered mechanical equipment may be dispersed beyond the construction site boundary, potentially affecting nearby residents living along Chancery Lane. As reported by the Contractor, corrective actions are being implemented immediately following the receipt of the emission complaint.
- As confirmed with GCL, all on-site machinery is operated on Ultra-Low Sulphur Diesel (ULSD), which is in with the statutory requirement in Hong Kong.
- As reported by GCL, diesel is directly filled into the machinery and there is no on-site storage of diesel oil. Air compressors are provided with drip trays and the motor crane and drilling machines were inspected with no diesel leakage observed.

*Mitigation Measures and Follow-up Actions Recommended to Contractor*

The Contractor has been recommended to implement measures to direct the diesel exhaust emissions away from the nearby sensitive receivers as far as practicable, particularly residents along Chancery Lane to the south and Old Bailey Street to the west of the construction site. According to the Contractor, mitigation measures have been implemented to facilitate the dilution of exhaust emissions and direct them away from nearby sensitive receivers (Figure 1):

- 1) Two ventilation fans have been installed near the exhaust of the air compressors where the exhaust emissions are directed towards the open space at Arbuthnot Wing via an air duct;
- 2) A ventilation fan has been installed to the exhaust of each of the three drilling machines on the north elevation of Block 17. The ventilation fans were connected to air ducts which divert the exhaust emissions to the north towards the Old Bailey Wing; and
- 3) The exhaust of the mobile crane was connected to an air duct through which exhaust emissions from the mobile crane were delivered to a drum filled with water.

The Contractor has been reminded to monitor any irregular and excessive exhaust emissions from all operating plant. The Contractor should ensure that there is no oil leakage from all operating machinery and provide drip trays where applicable. Additionally, the Contractor has been reminded to ensure that all mitigation measures as reported are properly implemented prior to operating any PME that is likely to cause considerable exhaust emissions. The Contractor has also been advised to notify all workers and operation supervisor of the emission complaint dated 23 November 2012.

Date of File Closed : 30 November 2012

Approved by:

ET Leader

IEC

JCCPS's  
Representative

Rocco Design  
Architect's  
Representative



(Name: Winnie Ko)  
Date: 30 November 2012



(Name: Sharifah Or)  
Date: 3 December 2012




(Name: C W Shaw)  
Date: 13 Dec 2012



(Name: CHARLES KUNG)  
Date: 23 Nov 2012

Gammon's  
Representative



(Name: Cliff Leung)  
Date: 30 Nov 2012

Annex L

Records of Vibration  
Monitoring for Trial Piling  
and Pipe/Bored Piling  
works

B.D. Ref. No. 屋宇署圖則編號  
 F.S.D. Ref. No. 消防處圖則編號  
 Revisions/修改/修訂  
 No. 編號 Description 說明 Date 日期 Approved 審批  
 - BD SUBMISSION 07/11 JS  
 A TENDER DRAWING 08/11 JS  
 B TENDER ADDENDUM 09/11 JS  
 C BD RE-SUBMISSION 09/11 JS

Plan Approved  
 NG Kiu-shing  
 Chief Structural Engineer  
 for BUILDING AUTHORITY  
 17 NOV 2011



**BD SUBMISSION**  
 Drawing Status 製圖狀況  
 - This drawing and the contents herein are the copyright of relevant consultants.  
 - 本圖紙及內容均受版權所屬有關顧問公司所有。  
 - No part of the drawing and the design contained herein may be reproduced without the prior written consent of relevant consultants.  
 - 本圖紙內任何部分均不得在未經有關顧問公司書面同意下，不得複製此圖紙內任何內容或設計。  
 - Do not take measurements directly from this drawing.  
 - 切勿直接從圖紙上量度尺寸。  
 - Check and verify all dimensions on site.  
 - 所有尺寸必須在工地現場檢查及核實。  
 - Read this drawing in conjunction with the specifications and all other related drawings.  
 - 此圖紙必須與規格說明書及其他有關圖紙一併閱讀。  
 - Notify the relevant consultants immediately of any discrepancy found herein.  
 - 如發現圖紙內有任何錯誤之處，應立即通知有關顧問公司。  
 Client 業主  
 香港賽馬會慈善信託基金  
 The Hong Kong Jockey Club Charities Trust


Design Consultant  
**HERZOG & DE MEURON**  
 Conservation Architect  
 Architect / AP  
**ROCCO**  
 Structural Engineer / RSE  
**ARUP**  
 Project 項目  
**CENTRAL POLICE STATION  
 CONSERVATION AND REVITALISATION**

Drawing Title 圖名  
**LAYOUT PLAN FOR SHAFT  
 GROUTED PILE FOUNDATION  
 (TRIAL PILE & MONITORING)**

Scale 比例 1:300(A1)  
 Drawing No. 圖號 F/005  
 Drawn 繪圖 K.C.Lai  
 Checked 校核 AL  
 Revision 修改版 C

WYAN KIN KEI  
 Chief Estimator / MICE ENGINEER  
 REGISTERED STRUCTURAL ENGINEER

Code file : 208474\_F005.dwg

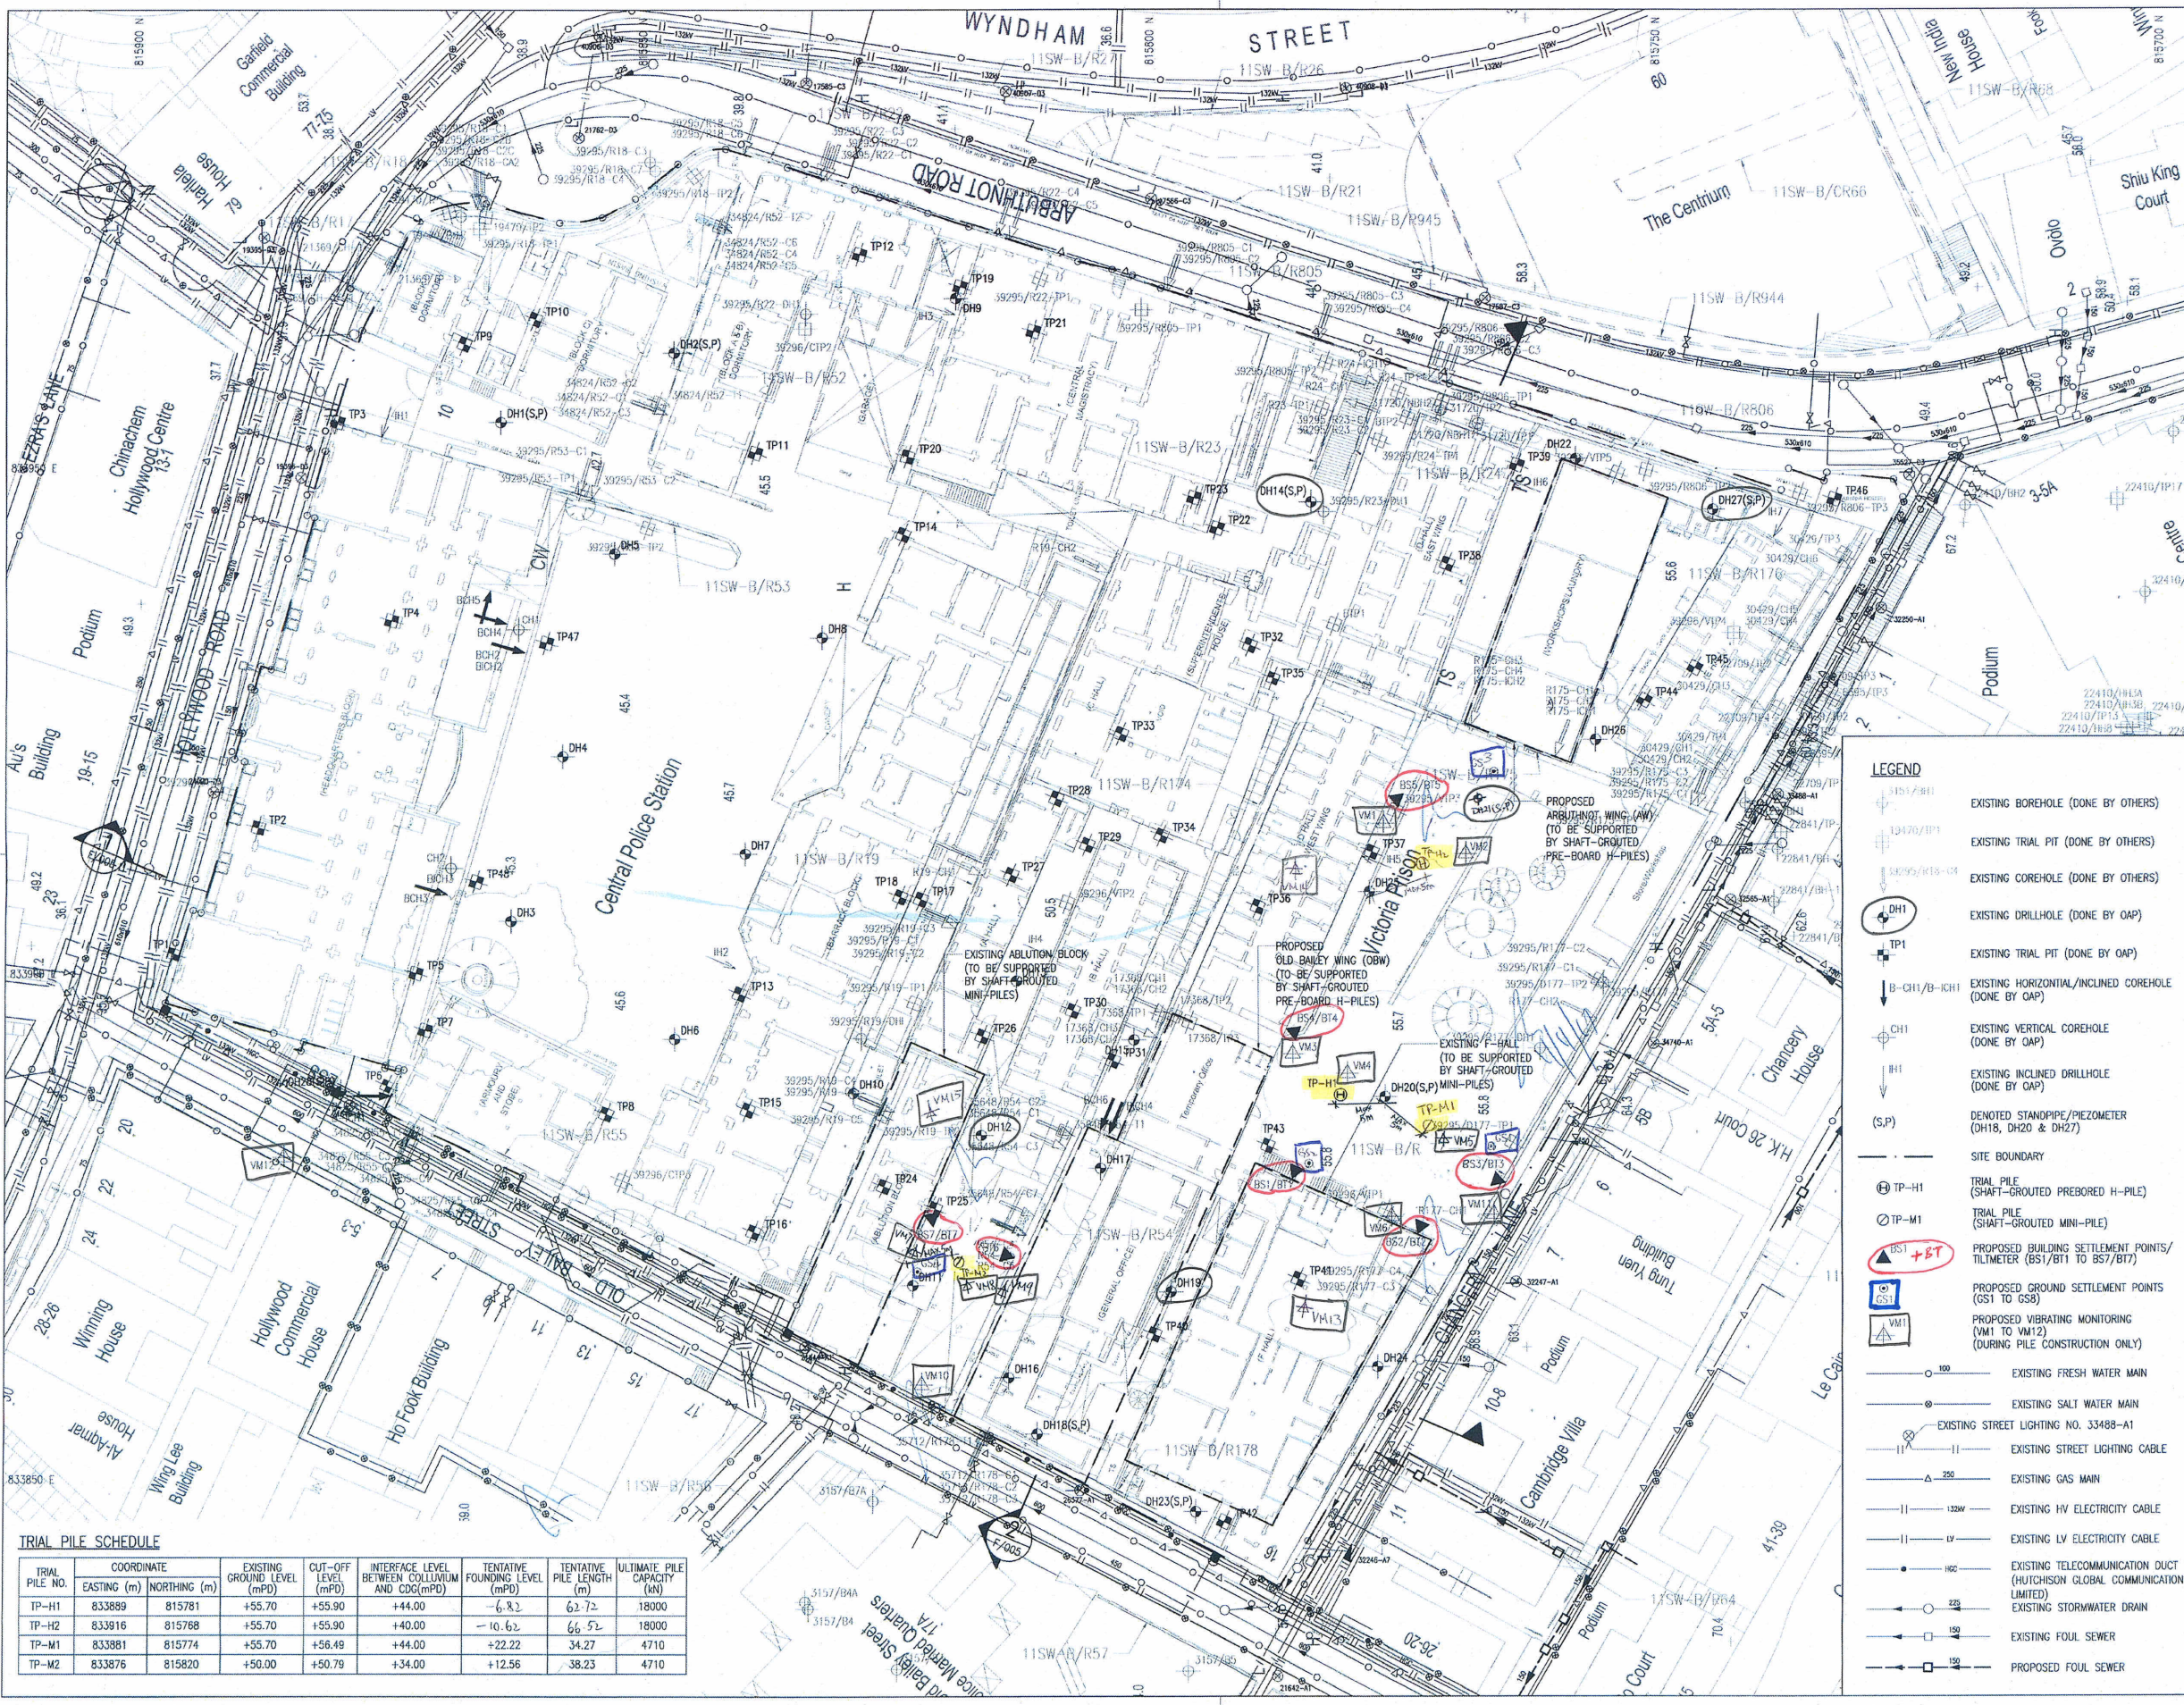

- LEGEND**
- BS1/B1
  - B1470/B17
  - BS295/R13-C1
  - DH1
  - TP1
  - B-CH1/B-ICH1
  - CH1
  - IH1
  - (S.P)
  - SITE BOUNDARY
  - TP-H1
  - TP-M1
  - BS1/BS7
  - GS1
  - VM1
  - 100
  - EXISTING FRESH WATER MAIN
  - EXISTING SALT WATER MAIN
  - EXISTING STREET LIGHTING NO. 33488-A1
  - EXISTING STREET LIGHTING CABLE
  - 250
  - EXISTING GAS MAIN
  - 1200V
  - EXISTING HV ELECTRICITY CABLE
  - LV
  - EXISTING LV ELECTRICITY CABLE
  - 100
  - EXISTING TELECOMMUNICATION DUCT (HUGHESON GLOBAL COMMUNICATIONS LIMITED)
  - 150
  - EXISTING STORMWATER DRAIN
  - 150
  - EXISTING FOUL SEWER
  - 150
  - PROPOSED FOUL SEWER
- EXISTING BOREHOLE (DONE BY OTHERS)
  - EXISTING TRIAL PIT (DONE BY OTHERS)
  - EXISTING COREHOLE (DONE BY OTHERS)
  - EXISTING DRILLHOLE (DONE BY OAP)
  - EXISTING TRIAL PIT (DONE BY OAP)
  - EXISTING HORIZONTAL/INCLINED COREHOLE (DONE BY OAP)
  - EXISTING VERTICAL COREHOLE (DONE BY OAP)
  - EXISTING INCLINED DRILLHOLE (DONE BY OAP)
  - DENOTED STANDPIPE/PIEZOMETER (DH18, DH20 & DH27)
  - TRIAL PILE (SHAFT-GROUTED PREBORED H-PILE)
  - TRIAL PILE (SHAFT-GROUTED MINI-PILE)
  - PROPOSED BUILDING SETTLEMENT POINTS/TILMETER (BS1/B1 TO BS7/B7)
  - PROPOSED GROUND SETTLEMENT POINTS (GS1 TO GS8)
  - PROPOSED VIBRATING MONITORING (VM1 TO VM12) (DURING PILE CONSTRUCTION ONLY)

**TRIAL PILE SCHEDULE**

TRIAL PILE NO.	COORDINATE		EXISTING GROUND LEVEL (mPD)	CUT-OFF LEVEL (mPD)	INTERFACE LEVEL BETWEEN COLLUMIUM AND CDC(mPD)	TENTATIVE FOUNDING LEVEL (mPD)	TENTATIVE PILE LENGTH (m)	ULTIMATE PILE CAPACITY (kN)
	EASTING (m)	NORTHING (m)						
TP-H1	833889	815781	+55.70	+55.90	+44.00	-6.83	62.72	18000
TP-H2	833916	815768	+55.70	+55.90	+40.00	-10.62	66.52	18000
TP-M1	833881	815774	+55.70	+56.49	+44.00	+22.22	34.27	4710
TP-M2	833876	815820	+50.00	+50.79	+34.00	+12.56	38.23	4710

RECEIVED BY  
 2011 SEP 19 P 2:54  
 R & D SECTION  
 BUILDINGS DEPARTMENT



恆誠建築工程有限公司

Win Win Way Construction Company Ltd.

(Trial pile) near Block 17

Monitoring Check Pts.	Trigger Levels		
	Alert level	Alarm level	Action level
Vibrating Monitoring	5mm/s	6mm/s	7.5mm/s

Vibration Record

Project Title: Central Police Station Conservation & Revitalization      Project No: WP201      21-Oct-2012      to      3-Nov-2012

POINT		VM1	VM2	VM3	VM4	VM5	VM6	VM7	VM8	VM9	VM10	VM11	VM12	VM13	VM14	VM15
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
2-Apr-2012	(Initial)	0.58	0.18	0.18	0.66	1.4	0.25	1.14	0.65	0.28	0.22	0.18	0.22	0.18	0.22	0.22
21-Oct-2012		Sunday														
22-Oct-2012		0.18	0.18	0.17	0.18	0.21	0.36	0.24	1.24	0.17	0.13	0.17	0.18	0.25	0.13	0.27
23-Oct-2012		Holiday														
24-Oct-2012		0.12	0.22	0.15	0.14	0.16	0.33	0.20	0.14	0.20	0.19	0.16	0.12	0.14	0.15	0.21
25-Oct-2012		0.32	0.15	0.27	0.26	0.13	0.25	0.14	0.14	0.12	0.21	0.13	0.15	0.23	0.12	0.12
26-Oct-2012		0.12	0.10	0.19	0.10	0.14	0.21	0.12	0.12	0.14	0.23	0.15	0.13	0.22	0.10	0.16
27-Oct-2012		0.25	0.18	0.16	0.16	0.16	0.22	0.16	0.17	0.15	0.16	0.76	0.14	0.18	0.19	0.14
28-Oct-2012		Sunday														
29-Oct-2012		0.16	1.25	0.19	0.29	0.18	0.18	0.18	0.13	0.23	0.16	0.15	0.16	0.16	0.17	0.14
30-Oct-2012		0.22	0.22	0.25	0.14	0.14	0.14	0.44	0.19	0.18	0.18	0.20	0.22	0.14	0.21	0.21
31-Oct-2012		0.13	0.15	0.26	0.18	0.14	0.13	0.13	0.14	0.13	0.14	0.15	0.22	0.12	0.13	0.12
1-Nov-2012		0.12	0.27	0.24	0.37	0.09	0.14	0.38	0.15	0.15	0.15	0.14	0.36	0.15	0.12	0.13
2-Nov-2012		0.33	0.21	0.18	0.15	0.12	0.14	0.46	0.14	0.15	0.15	0.14	0.13	0.16	0.12	0.18
3-Nov-2012		0.87	0.14	0.22	0.15	0.89	0.66	0.12	0.13	0.66	0.12	0.13	0.12	0.15	0.14	0.11


Prepared by : Lo wing yue (Surveyor)

Monitoring Check Pts.	Trigger Levels		
	Alert level	Alarm level	Action level
Vibrating Monitoring	5mm/s	6mm/s	7.5mm/s

### Vibration Record

Project Title: Central Police Station Conservation & Revitalization      Project No: WP201      4-Nov-2012      to      17-Nov-2012

POINT	VM1	VM2	VM3	VM4	VM5	VM6	VM7	VM8	VM9	VM10	VM11	VM12	VM13	VM14	VM15	
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	
2-Apr-2012 (Initial)		0.58	0.18	0.18	0.66	1.4	0.25	1.14	0.65	0.28	0.22	0.18	0.22	0.18	0.22	0.22
4-Nov-2012		Sunday														
5-Nov-2012		0.12	0.13	0.13	0.26	0.15	0.14	0.14	0.25	0.15	0.14	0.20	0.22	0.28	0.13	0.12
6-Nov-2012		0.10	0.17	0.18	0.14	0.22	0.23	0.20	0.30	0.15	0.15	0.23	0.13	0.10	0.13	Blocked
7-Nov-2012		0.20	0.14	0.14	0.14	0.25	0.14	0.29	0.14	0.16	0.51	0.14	0.15	0.25	0.10	Blocked
8-Nov-2012		0.13	0.15	0.13	0.15	0.34	0.10	0.93	0.73	0.85	0.57	0.51	0.15	0.22	0.21	Blocked
9-Nov-2012		0.12	0.24	0.24	0.29	0.11	0.14	0.34	0.32	0.12	0.22	0.26	0.20	0.33	0.11	Blocked
10-Nov-2012		0.24	0.19	0.12	0.29	0.14	0.13	0.36	0.46	0.91	0.65	0.14	0.39	0.67	0.12	Blocked
11-Nov-2012		Sunday														
12-Nov-2012		0.15	0.15	0.16	0.38	0.23	0.17	0.31	0.14	0.19	0.15	0.19	0.16	0.27	0.29	Blocked
13-Nov-2012		0.13	0.12	0.12	0.54	0.12	0.13	0.35	0.23	0.27	0.18	0.12	0.31	0.43	0.11	Blocked
14-Nov-2012		0.13	0.23	0.22	0.18	0.15	0.14	0.29	0.13	0.24	0.14	0.32	0.20	0.15	0.15	Blocked
15-Nov-2012		0.23	0.33	0.20	0.25	0.19	0.23	0.14	0.25	0.21	0.36	0.19	0.13	0.21	0.33	Blocked
16-Nov-2012		0.13	0.16	0.27	0.48	0.29	0.26	0.15	0.15	0.35	0.19	0.13	0.12	0.35	0.14	Blocked
17-Nov-2012		0.29	0.16	0.15	0.15	0.26	0.15	0.22	0.15	0.18	0.20	0.15	0.15	0.17	0.20	Blocked



恆誠建築工程有限公司

Win Win Way Construction Company Ltd.

Monitoring Check Pts.	Trigger Levels		
	Alert level	Alarm level	Action level
Vibrating Monitoring	5mm/s	6mm/s	7.5mm/s

### Vibration Record

Project Title: Central Police Station Conservation & Revitalization      Project No: WP201      18-Nov-2012      to      1-Dec-2012

POINT		VM1	VM2	VM3	VM4	VM5	VM6	VM7	VM8	VM9	VM10	VM11	VM12	VM13	VM14	VM15
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
2-Apr-2012	(Initial)	0.58	0.18	0.18	0.66	1.4	0.25	1.14	0.65	0.28	0.22	0.18	0.22	0.18	0.22	0.22
18-Nov-2012																
Sunday																
19-Nov-2012		0.13	0.14	0.13	0.15	0.14	0.14	0.28	0.13	0.12	0.12	0.13	0.15	0.14	0.13	Blocked
20-Nov-2012		0.21	0.11	0.13	0.10	0.13	0.15	0.22	0.14	0.14	0.26	0.13	0.23	0.21	0.14	Blocked
21-Nov-2012		0.18	0.14	0.11	0.18	0.27	0.14	0.15	0.13	0.14	0.16	0.13	0.11	0.11	0.15	Blocked
22-Nov-2012		0.18	0.11	0.12	0.13	0.14	0.22	0.13	0.16	0.21	0.12	0.13	0.14	0.26	0.18	Blocked
23-Nov-2012		0.15	0.12	0.16	0.13	0.15	0.19	0.12	0.10	0.13	0.14	0.22	0.24	0.14	0.14	Blocked
24-Nov-2012		0.11	0.14	0.15	0.14	0.15	0.15	0.15	0.10	0.14	0.57	0.12	0.10	0.11	0.13	Blocked
25-Nov-2012																
Saturday																
26-Nov-2012		0.45	0.12	0.14	0.11	0.11	0.13	0.14	0.13	0.13	0.15	0.26	0.11	0.11	0.20	Blocked
27-Nov-2012		0.23	0.13	0.15	0.17	0.18	0.19	0.14	0.14	0.17	0.09	0.58	0.17	0.21	0.12	Blocked
28-Nov-2012		0.14	0.14	0.15	0.14	0.13	0.14	0.14	0.12	0.15	0.14	0.15	0.14	0.17	0.14	Blocked
29-Nov-2012		0.14	0.14	0.14	0.14	0.14	0.15	0.13	0.14	0.14	0.11	0.22	0.14	0.17	0.16	Blocked
30-Nov-2012		0.20	0.13	0.12	0.12	0.21	0.82	0.14	0.13	0.14	0.28	0.11	0.10	0.14	0.11	Blocked
1-Dec-2012		0.24	0.15	0.14	0.16	0.15	0.13	0.16	0.12	0.28	0.25	0.14	0.22	0.14	0.12	Blocked

Prepared by : Lo wing yue (Surveyor)





U.D. Ref. No. 工程圖則編號  
 3/3053/11 (B/LK 173.56) (H.C.) (S)  
 F.S.D. Ref. No. 測量圖則編號

Revision/Submission 修改版/報建

No. 編號	Description 說明	Date 日期	Approved 簽定
-	BD SUBMISSION	12/11	JS

Plan Approved

NG Kin-shing  
 Chief Structural Engineer  
 for BUILDING AUTHORITY  
 20 FEB 2012



**BD SUBMISSION**  
 Drawing Status 製圖狀況

This drawing and the contents herein are the copyright of relevant consultants.  
 本圖紙及其內容版權歸有關顧問公司所有。

No part of the drawing and the design contained herein may be reproduced without the prior written consent of relevant consultants.  
 未經有關顧問公司書面同意，不得複製圖紙內容或任何內容或設計。

Do not take measurements directly from this drawing  
 切勿直接從圖紙上量取尺寸。

Check and verify dimensions on site.  
 所有尺寸必須在工地現場校核及覆核。

Read this drawing in conjunction with the specifications and all other related drawings.  
 此圖紙必須與說明書及其他有關圖紙一併閱讀。

Notify the relevant consultants immediately of any discrepancy found herein.  
 如發現有任何錯誤之處，應立即通知有關顧問公司。

Client 業主

賽馬會文物保育有限公司  
 The Jockey Club CPS Limited

Design Consultant  
**HERZOG & DEMELRON**

Conservation Architect  
**HUTCHISON GLOBAL COMMUNICATIONS LIMITED**

Executive Architect / AP  
**ROCCO**  
 許李平

Structural Engineer / RSE  
**ARUP**  
 E & M Engineer  
**JRP**

Project 項目  
**CENTRAL POLICE STATION  
 CONSERVATION AND REVITALISATION  
 PROJECT**

Drawing Title 圖名  
**MONITORING LAYOUT PLAN**

Scale 比例  
 1:300@A1

Drawn 繪圖  
 K.C.Loi

Checked 校對  
 AL

Revision 修改版  
 00-OAP209674-G-001

- LEGEND**
- EXISTING FRESH WATER MAIN
  - EXISTING SALT WATER MAIN
  - EXISTING STREET LIGHTING NO. 33498-A1
  - EXISTING STREET LIGHTING CABLE
  - EXISTING GAS MAIN
  - EXISTING HV ELECTRICITY CABLE
  - EXISTING LV ELECTRICITY CABLE
  - EXISTING TELECOMMUNICATION DUCT (HUTCHISON GLOBAL COMMUNICATIONS LIMITED)
  - EXISTING STORMWATER DRAIN
  - EXISTING FOUL SEWER
  - PROPOSED FOUL SEWER
  - SITE BOUNDARY
  - EXISTING RETAINING WALL
  - ▲ DH1(S,P) EXISTING DRILLHOLE WITH STANDPIPE/PIEZOMETER
  - ▲ BS1-1/BT1-1 PROPOSED BUILDING SETTLEMENT POINTS/TILMETER
  - ▲ RS174-1/RT174-1 PROPOSED RETAINING WALL SETTLEMENT POINTS/TILMETER
  - ▲ IN1-1 PROPOSED INCLINOMETER TO BE BUILT IN BORED PILE OR PIPE PILE WALL
  - GS1 PROPOSED GROUND SETTLEMENT POINTS
  - UT1 PROPOSED UTILITY MONITORING POINTS
  - ▲ VM1-1 PROPOSED VIBRATION MONITORING POINTS
  - ADH1(S,P) PROPOSED ADDITIONAL DRILLHOLE

NOTES

UTILITIES SETTLEMENT POINTS (UT1 TO UT6) SHALL ONLY BE INSTALLED AFTER EXCAVATION PERMIT IS OBTAINED AS ALTERNATIVE SETTLEMENT POINTS (GS1 TO GS6) MAY BE INSTALLED.

SHOULD UT1 TO UT6 BE INSTALLED AS IS AND GS1 TO GS6 SHALL NOT BE REQUIRED.

EITHER UTILITIES SETTLEMENT MARKERS (UT1 TO UT6) OR GROUND SETTLEMENT MARKERS (GS1 TO GS6) SHOULD BE INSTALLED PRIOR TO THE COMMENCEMENT OF OLD BAILEY WING PLS WORKS.

RECEIVED BY  
 281 DEC 23 P 2:09  
 R & D Section  
 PLANNING DEPARTMENT

( Bored Pile Walls / Pipe Pile Walls at Block 50 )



Monitoring Check Pts.	Trigger Levels		
	Alert level	Alarm level	Action level
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s
Vibration at largest span of highest Structural level	5.0mm/s	6.0mm/s	7.5mm/s

### Vibration Record

Project Title: Central Police Station Conservation & Revitalization      Project No: WP201      21-Oct-2012      to      3-Nov-2012

POINT		VM8-1	VM11-1	VM11-2	VM12-1	VM12-2	VM14-3	VM17-1	VM17-2	VM17-3
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
19-Jun-2012	(Initial)	<b>0.56</b>	<b>0.13</b>	<b>0.19</b>	<b>0.22</b>	<b>0.13</b>	<b>0.21</b>	<b>0.13</b>	<b>0.13</b>	<b>0.37</b>
Surveying Date										
21-Oct-2012		Sunday								
22-Oct-2012		0.21	0.20	0.17	0.19	0.17	0.19	0.18	0.16	0.25
23-Oct-2012		Holiday								
24-Oct-2012		0.25	0.22	0.27	0.17	0.26	0.16	0.14	0.15	0.13
25-Oct-2012		0.16	0.23	0.18	0.22	0.30	0.20	0.15	0.18	0.22
26-Oct-2012		0.17	0.22	0.14	0.23	0.17	0.12	0.11	0.13	0.13
27-Oct-2012		0.15	0.16	0.18	0.16	0.15	0.24	0.15	0.16	0.16
28-Oct-2012		Sunday								
29-Oct-2012		0.12	1.60	0.17	0.12	0.17	0.24	0.15	1.25	0.40
30-Oct-2012		0.22	0.14	0.23	0.22	0.14	0.15	0.19	0.25	0.16
31-Oct-2012		0.10	0.13	0.13	0.10	0.12	0.14	0.10	0.12	0.13
1-Nov-2012		0.31	0.28	0.14	0.22	0.25	0.24	0.19	0.19	0.35
2-Nov-2012		0.29	0.13	0.23	0.13	0.16	0.14	0.09	0.12	0.14
3-Nov-2012		0.12	0.14	0.09	0.10	0.11	0.47	0.10	0.11	0.89

( Bored Pile Walls / Pipe Pile Walls at Block 50 )

**WW** 恆誠建築工程有限公司  
Win Win Way Construction Company Ltd.

Monitoring Check Pts.	Trigger Levels		
	Alert level	Alarm level	Action level
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s
Vibration at largest span of highest Structural level	5.0mm/s	6.0mm/s	7.5mm/s

### Vibration Record

Project Title: Central Police Station Conservation & Revitalization      Project No: WP201      4-Nov-2012      to      17-Nov-2012

POINT		VM8-1	VM11-1	VM11-2	VM12-1	VM12-2	VM14-3	VM17-1	VM17-2	VM17-3
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
19-Jun-2012 (Initial)		<b>0.56</b>	<b>0.13</b>	<b>0.19</b>	<b>0.22</b>	<b>0.13</b>	<b>0.21</b>	<b>0.13</b>	<b>0.13</b>	<b>0.37</b>
Surveying Date										
4-Nov-2012		Sunday								
5-Nov-2012		0.22	0.23	0.11	0.30	0.13	0.14	0.24	0.45	0.31
6-Nov-2012		0.31	0.20	0.30	0.25	0.16	0.32	0.13	0.30	0.16
7-Nov-2012		0.09	0.19	0.27	0.30	0.27	0.15	0.20	0.17	0.13
8-Nov-2012		Blocked	0.15	0.14	0.14	0.28	0.14	0.16	0.14	0.28
9-Nov-2012		Blocked	0.17	0.20	0.32	0.15	0.27	0.14	0.30	0.29
10-Nov-2012		Blocked	0.14	0.14	0.17	0.21	0.14	0.40	0.39	0.38
11-Nov-2012		Sunday								
12-Nov-2012		Blocked	0.22	0.22	0.26	0.14	0.15	0.15	0.14	0.14
13-Nov-2012		Blocked	0.14	0.30	0.52	0.23	0.29	0.36	0.26	0.12
14-Nov-2012		Blocked	0.13	0.14	0.29	0.20	0.14	0.15	0.10	0.34
15-Nov-2012		Blocked	0.36	0.13	0.19	0.32	0.26	0.12	0.25	0.13
16-Nov-2012		Blocked	0.10	0.13	0.22	0.33	0.35	0.28	0.18	0.15
17-Nov-2012		Blocked	0.21	0.18	0.23	0.23	0.15	0.13	0.25	0.22

Prepared by : Lo wing yue (Surveyor)

Monitoring Check Pts.	Trigger Levels		
	Alert level	Alarm level	Action level
Vibration Monitoring	2mm/s	2.5mm/s	3mm/s
Vibration at largest span of highest Structural level	5.0mm/s	6.0mm/s	7.5mm/s

### Vibration Record

Project Title: Central Police Station Conservation & Revitalization      Project No: WP201      18-Nov-2012      to      1-Dec-2012

POINT		VM8-1	VM11-1	VM11-2	VM12-1	VM12-2	VM14-3	VM17-1	VM17-2	VM17-3
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
19-Jun-2012	(Initial)	<b>0.56</b>	<b>0.13</b>	<b>0.19</b>	<b>0.22</b>	<b>0.13</b>	<b>0.21</b>	<b>0.13</b>	<b>0.13</b>	<b>0.37</b>
Surveying Date										
18-Nov-2012		Sunday								
19-Nov-2012		Blocked	0.13	0.23	0.14	0.15	0.28	0.16	0.12	0.22
20-Nov-2012		Blocked	0.12	0.14	0.18	0.14	0.24	0.14	0.12	0.15
21-Nov-2012		Blocked	0.18	0.14	0.24	0.14	0.13	0.16	0.11	0.15
22-Nov-2012		Blocked	0.25	0.13	0.23	0.14	0.20	0.12	0.17	0.19
23-Nov-2012		Blocked	0.11	0.14	0.16	0.17	0.17	0.14	0.20	0.15
24-Nov-2012		Blocked	0.14	0.12	0.13	0.14	0.11	0.14	0.11	0.11
25-Nov-2012		Sunday								
26-Nov-2012		Blocked	0.29	0.12	0.12	0.11	0.12	0.18	0.30	0.13
27-Nov-2012		Blocked	0.20	0.26	0.23	0.18	0.12	0.25	0.42	0.25
28-Nov-2012		Blocked	0.17	0.15	0.22	0.22	0.14	0.15	0.11	0.14
29-Nov-2012		Blocked	0.12	0.13	0.19	0.13	0.12	0.14	0.10	0.11
30-Nov-2012		Blocked	0.29	0.20	0.22	0.15	0.20	0.15	0.23	0.30
1-Dec-2012		Blocked	0.20	0.27	0.25	0.22	0.14	0.17	0.33	0.31

Annex M

Records of Vibration  
Monitoring for Other  
Construction Works




110 Ref No: 1/7/2/2/2/2/2

Revision/Comments (Date) (Rev)

No. Rev	Description	Date	By	Appr
1	ED SUBMISSION	12/11	JS	

Plan Approved

NG Kwan  
Chief Structural Engineer  
for the BUILDING AUTHORITY  
20 FEB 2012



**BD SUBMISSION**  
Drawing Status: REVISION

This drawing and its contents form and the copyright of relevant documents shall remain the property of HERZOG & DEMEUREN.

No part of this drawing and the design contained herein may be reproduced, stored in a retrieval system or transmitted in any form or by any means, electronic, mechanical, photocopying, recording, or otherwise, without the prior written consent of HERZOG & DEMEUREN.

Do not take measurements directly from this drawing without the written consent of HERZOG & DEMEUREN.

Do not scale drawings unless specifically stated.

Check and verify all dimensions on site.

Read this drawing in conjunction with the specifications and all other related drawings.

Make the relevant consultant immediately of any discrepancy found from the drawings.

Client 客户  
香港有线网络有限公司  
The Jockey Club Ltd

Design Consultant  
**HERZOG & DEMEUREN**  
Conservation Architect  
香港城市大学建筑学院  
Executive Architect FAP  
**ROCCO**  
Structural Engineer / RSE  
**ARUP**  
Conservation Architect  
**JRP**

Project Title  
**CENTRAL POLICE STATION  
CONSERVATION AND REVITALISATION  
PROJECT**

Drawing Title 图名  
**MONITORING LAYOUT PLAN**

Scale 比例尺  
1:5000A1

Drawn 绘图  
K.C.L.

Checked 校核  
M.

Revision 修订  
Revision ID 修订号  
**00-OAP209674-G-001**


- LEGEND**
- EXISTING FRESH WATER MAIN
  - EXISTING SALT WATER MAIN
  - EXISTING STREET LIGHTING NO. 33489-A1
  - EXISTING STREET LIGHTING CABLE
  - EXISTING GAS MAIN
  - EXISTING HV ELECTRICITY CABLE
  - EXISTING LV ELECTRICITY CABLE
  - EXISTING TELECOMMUNICATION DUCT (HONGKONG GLOBAL COMMUNICATIONS LIMITED)
  - EXISTING STORMWATER DRAIN
  - EXISTING FOUR SEWER
  - PROPOSED FOUR SEWER
  - SITE BOUNDARY
  - EXISTING RETAINING WALL
  - ⊕ DH1(S/P) EXISTING DRILLHOLE WITH STAMP/PEZOMETER
  - ▲ BS1-1/BS1-1 PROPOSED BUILDING SETTLEMENT POINTS/INCLINOMETER
  - ▲ BS174-1/BS174-1 PROPOSED RETAINING WALL SETTLEMENT POINTS/INCLINOMETER
  - ⊕ BS1-1 PROPOSED INCLINOMETER TO BE INSTALLED TO DETECT FILL WALL OR OTHER FILL WALL
  - ⊕ GS1 PROPOSED GROUND SETTLEMENT POINTS
  - ⊕ UT1 PROPOSED UTILITY MONITORING POINTS
  - ⊕ VM-1 PROPOSED VIBRATION MONITORING POINTS
  - ⊕ ADH1(S/P) PROPOSED ADDITIONAL DRILLHOLE

NOTES

1. ALL POINTS TO BE SET AT POINTS (LEFT TO RIGHT) SHOWN ON THE MONITORING POINTS LOCATION PLAN TO BE INSTALLED AS ALTERNATIVE SETTLEMENT POINTS (SEE PHOTO) TO BE INSTALLED.

2. SETTING OUT TO BE COMPLETED WITHIN 60 DAYS OF THE COMMENCEMENT OF THE WORKS.

3. SETTLEMENT MONITORING POINTS (LEFT TO RIGHT) TO BE FOLLOWED BY SETTLEMENT MONITORING POINTS (LEFT TO RIGHT) SHALL BE INSTALLED PRIOR TO COMMENCEMENT OF THE WORKS.

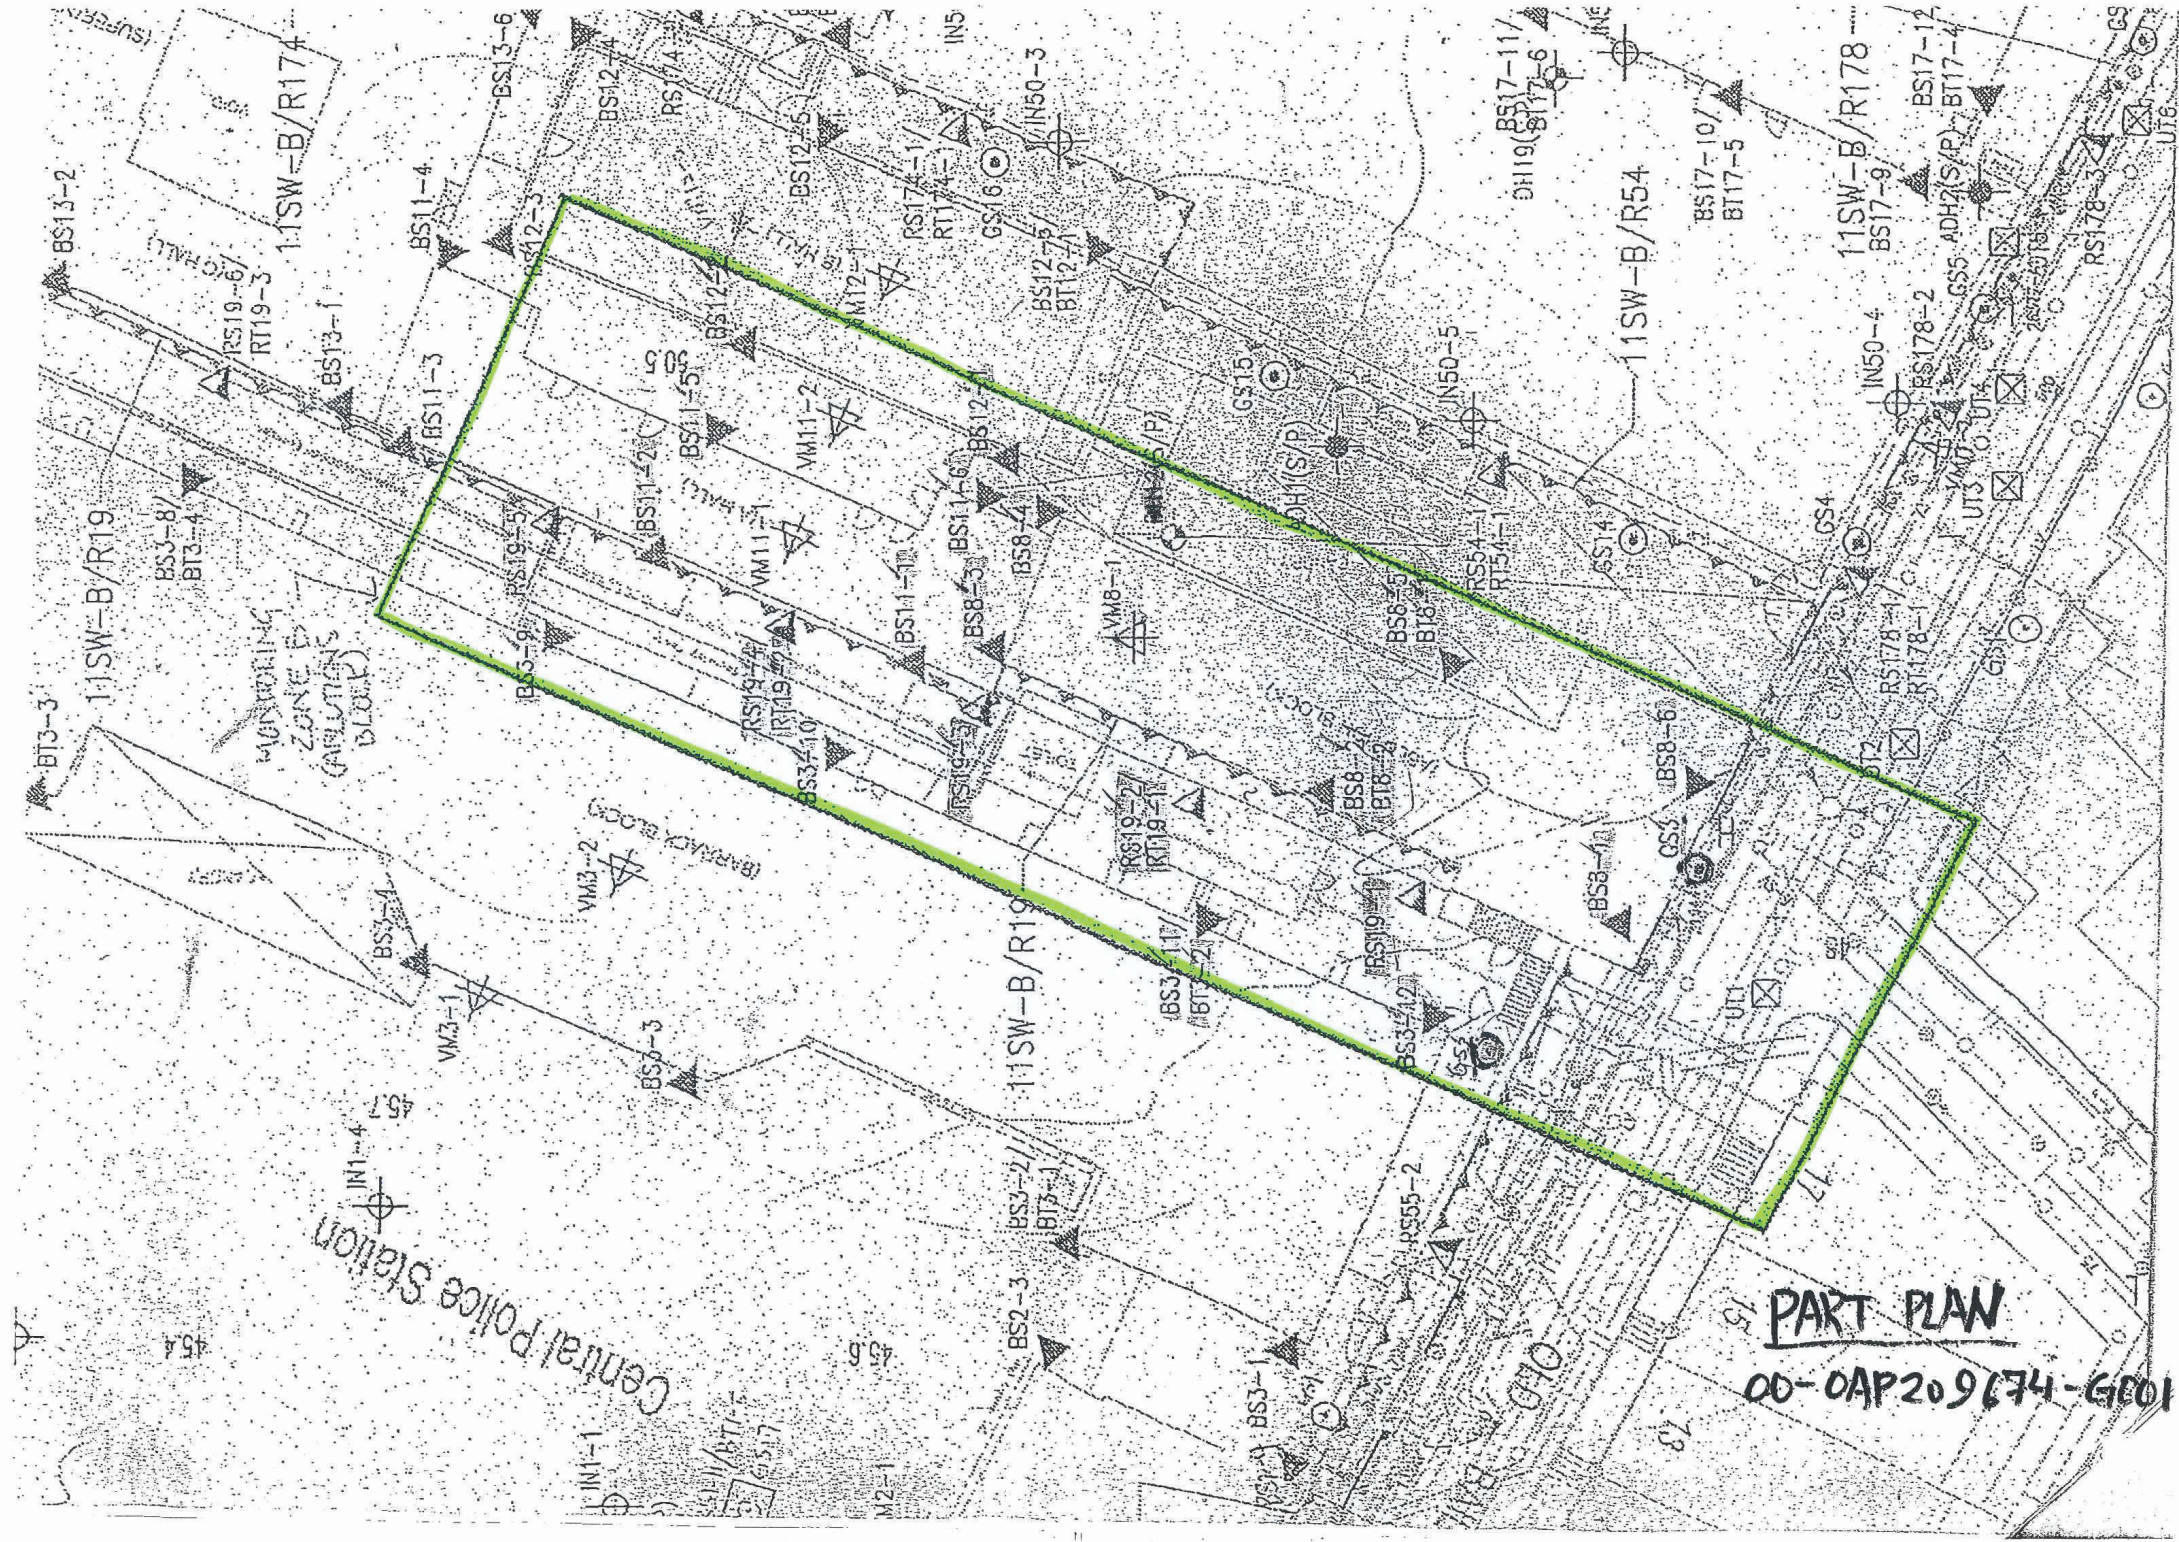

Central Police Station

MONITORING ZONE (ASPHALTIONS BLOWN)

PART PLAN

10015-147360240-00







仁利建築有限公司  
Yan Lee Construction Co., Ltd.

Monitoring Check Pts.	Trigger Levels		
	Alert level	Alarm level	Action level
Vibrating Monitoring	2mm/s	2.5mm/s	3mm/s

Vibration Record

Project Title: Central Police Station Conservation & Revitalization Project No: WP203 Date: 4-11-2012 To 17-11-2012

POINT		VM8-1	VM11-1	VM11-2												
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
23-Apr-12 (Initial)		0.212	0.087	0.116												
4-Nov-2012																
5-Nov-2012		0.656	0.284	0.170												
6-Nov-2012		1.450	0.700	0.438												
7-Nov-2012		0.238	0.249	0.217												
8-Nov-2012		0.398	0.094	0.591												
9-Nov-2012		0.270	0.102	0.178												
10-Nov-2012		0.273	0.136	0.146												
11-Nov-2012																
12-Nov-2012		0.601	0.102	0.236												
13-Nov-2012		0.386	0.176	0.232												
14-Nov-2012		0.762	0.242	0.331												
15-Nov-2012		1.430	0.305	0.212												
16-Nov-2012		0.334	0.162	0.341												
17-Nov-2012		1.110	0.116	0.270												

Prepared by : Cheung Wai Ching (Leveller)



仁利建築有限公司  
Yan Lee Construction Co., Ltd.

Monitoring Check Pts.	Trigger Levels		
	Alert level	Alarm level	Action level
Vibrating Monitoring	2mm/s	2.5mm/s	3mm/s

### Vibration Record

Project Title: Central Police Station Conservation & Revitalization

Project No: WP203

Date: 18-11-2012 to 1-12-2012

POINT		VM8-1	VM11-1	VM11-2												
DATE	PD/(m)	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s	mm/s
23/4/2012	(Initial)	0.212	0.087	0.116												
18-11-2012																
19-11-2012		0.170	0.151	0.212												
20-11-2012		0.207	0.094	0.111												
21-11-2012		0.471	0.120	0.143												
22-11-2012		0.144	0.093	0.102												
23-11-2012		0.605	0.137	0.263												
24-11-2012		0.447	0.297	1.010												
25-11-2012																
26-11-2012		0.621	0.317	0.450												
27-11-2012		0.215	0.108	0.217												
28-11-2012		0.226	0.105	0.159												
29-11-2012		1.020	0.602	0.177												
30-11-2012		0.304	0.139	0.218												
1-12-2012		0.463	0.112	0.178												

清

Prepared by: CHEUNG WAI CHING (Leveler)
