Civil Engineering and Development Department

Contract No. ST/2013/01 Sha Tin New Town Stage II Road T3 and Associated Roadworks – Remaining Works, Phase III

Monthly EM&A Report

(Version 1.0) November 2015

Certified By	(Environmental Team Leader)
REMARKS:	

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

CINOTECH CONSULTANTS LTD Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong Tel: (852) 2151 2083 Fax: (852) 3107 1388 Email: info@cinotech.com.hk

TABLE OF CONTENTS

	F	Page	;
EX	ECUTIVE SUMMARY	1	
Int	roduction	1	
En	vironmental Monitoring and Audit Works	1	
	vironmental Licenses and Permits		
	y Information in the Reporting Month		
Fut	ture Key Issues	2	
1	INTRODUCTION	4	
Ba	ckground	4	
Co	nstruction Programme	5	
Su	mmary of EM&A Requirements	5	
2	NOISE MONITORING	6	
Mc	onitoring Requirements	6	,
	onitoring Locations		
Mo	onitoring Equipment	6	1
	onitoring Parameters, Frequency and Duration		
	onitoring Methodology and QA/QC Procedures		
Re	sults and Observations	7	
3	ENVIRONMENTAL AUDIT	9	Į
Sit	e Audits	9	1
Re	view of Environmental Monitoring Procedures	9	i
	tus of Environmental Licensing and Permitting		
	tus of Waste Management		
	plementation Status of Environmental Mitigation Measures		
	mmary of Exceedance		
	plementation Status of Event Action Plans mmary of Complaint and Prosecution		
4	FUTURE KEY ISSUES		
-			
	onitoring Schedule for the Next Month nstruction Program for the Next Month		
5	CONCLUSIONS AND RECOMMENDATIONS	14	
	nclusions		

LIST OF TABLES

Table I	Summary Table for Events Recorded in the Reporting Month
Table II	Summary Table for Key Information in the Reporting Month
Table III	Key Information in the EIA Report and the Status of EMIS
Table 1.1	Key Project Contacts
Table 2.1	Location of Noise Monitoring Station
Table 2.2	Noise Monitoring Equipment
Table 2.3	Noise Monitoring Parameters, Frequency and Duration
Table 2.4	Baseline Noise Level and Allowed Construction Noise Level for Monitoring
	Station

Table 2.5Summary Table of Noise Monitoring Results during the Reporting Month

Table 3.1	Summary of Environmental Licensing and Permit Status
-----------	--

Table 3.2Observations and Recommendations of Site Audit

LIST OF FIGURE

- Figure 1 Site Layout Plan with location of Noise Monitoring Station
- Figure 2 ET's Organization Chart

LIST OF APPENDICES

- Appendix A Action and Limit Level
- Appendix B Copies of Calibration Certificates
- Appendix C Environmental Monitoring Schedules
- Appendix D Noise Monitoring Results and Graphical Presentations
- Appendix E Summary of Exceedance
- Appendix F Site Audit Summary
- Appendix G Event Action Plan
- Appendix H Updated Environmental Mitigation Implementation Schedule
- Appendix I Waste Generation in the Reporting Month
- Appendix J Complaint Log
- Appendix K Construction Programme

EXECUTIVE SUMMARY

Introduction

- 1. This is the 18th monthly Environmental Monitoring and Audit (EM&A) Report prepared by Cinotech Consultants Limited for CEDD Contract No. ST/2013/01 "Sha Tin New Town Stage II, Road T3 and Associated Roadworks – Remaining Works, Phase III" (hereinafter referred to as 'the Project'). This report documents the findings of EM&A Works conducted in November 2015.
- 2. The major site activities undertaken in the reporting month included:
 - Road marking modification
 - Re-surfacing
 - Repaving the cycle-track
 - Drainage and irrigation pipe laying
 - Hydroseeding

Environmental Monitoring and Audit Works

- 3. Environmental monitoring and audit works for the Project were performed regularly and the results were checked and reviewed. Site audits were conducted once per week. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.
- 4. Summary of the non-compliance of the reporting month is tabulated in **Table I**.

Table ISummary Table for Events Recorded in the Reporting Month

Donomotor	No. of Exceedance		No. of Exceedance	A stion Taken	
Parameter	Action Level	Limit Level	Due to this Project	Action Taken	
Noise	0	2*	0	N/A	

*Exceedances occurred in the noise monitoring during the restricted hours (19:00-23:00hrs and 23:00-07:00 hrs) conducted for the evening and night-time construction works from 18th to 21st November 2015. No direct evidence showing that the exceedances were due to the Project as the measured impact noise level is influenced by nearby road traffic noise. Details of the exceedance investigation are given in **Appendix E**.

Construction Noise

5. All construction noise monitoring was conducted as scheduled in the reporting month. Two Limit Level exceedances were recorded.

Environmental Licenses and Permits

6. Environmental related licenses/permits granted to the Project include the Environmental Permit (EP) for the Project and the Water Discharge Licence.

Key Information in the Reporting Month

7. Summary of key information in this reporting month is tabulated in **Table II**. The key information in the EIA Report is summarized in the Table III below. According to the

EIA Report, air quality and noise would be the key environmental issues during the construction of the Project. Details of the implementation of mitigation measures are provided in the **Appendix H**.

Event	Event Details		Action Taken	Status	Remark
Event	Number	Nature	ure Action Taken		Kelliark
Complaint received	0		N/A	N/A	
Changes to the assumptions and key construction / operation activities recorded	0		N/A	N/A	
Status of submissions under EP	1	Monthly EM&A Report for (October 2015)	Submitted to EPD on 19 th November 2015.	N/A	
Notifications of any summons & prosecutions	0		N/A	N/A	

Future Key Issues

Major site activities for the coming month will include:

- Drainage laying
- Bicycle stands construction
- Hydroseeding
- Trees/ shrubs planting

The anticipated major environmental issues will be mainly on silty surface runoff, blocking of drainage system and ponding water during rainy season; and dust and noise nuisance due to roadwork activities.

2

r	Table III Key Information in the EIA Report and the Status of EMIS							
	Issues	Assumptions and Assessment	Recommended Mitigation Measures	Status of Implementation of Mitigation Measures				
	Air	With the implementation of dust suppression mitigation measures, the level of construction dust would comply with the relevant AQO.	Watering the work area at least twice a day. Environmental pollution control measures for minimizing construction dust impact as stipulated in the APCO.	During the audit sessions, it was observed that:Watering the work site was provided.				
Se	Noise	Noise level at most of NSRs would exceed the noise criteria without mitigation measures.	Good site practices, adoption of quiet construction plant, reduction of on-time operation of plant, movable noise barrier, avoid simultaneous noisy activities.	Duringtheauditsessions,itwasobserved that:.• Simultaneousnoisyactivitieswereavoided				
Construction Phase	Water	The potential impact rose from the construction of flyovers spanning to the upper Shing Mun River Channel.	Construction works spanning the upper Shing Mun River should be undertaken in the dry season All storm runoff should be routed through oil/grit separators and/or sediment basins/traps before being allowed to be discharged into the nearby receiving waters. All stockpiled areas should be covered. All sediment removable facilities should be maintained and the deposited sediments should be removed regularly.	The construction of flyovers spanning to the upper Shing Mun River Channel was completed under Sha Tin New Town – Stage II, Trunk Road T3 Project in 2009				

Table III Key Information in the EIA Report and the Status of EMIS

1 INTRODUCTION

Background

- 1.1 'Road T3 and Associated Roadworks Remaining Works, Phase III' Project (hereinafter referred to as "the Project") is the remaining works of the Project 'Sha Tin New Town – Stage II, Trunk Road T3 (Tai Wai)' which is a Schedule 2 Designated Project under the Environmental Impact Assessment Ordinance (Cap. 449). A study of environmental impact assessment (EIA) was undertaken for the 'Sha Tin New Town – Stage II, Trunk Road T3 (Tai Wai)' to consider the key issues of to provide information on nature and extent of environmental impacts arising from the construction and operation of Road T3, and identify possible mitigation measures associated with the works. An EIA Report was approved by the Environmental Protection Department (EPD) on March 1998.
- 1.2 The Project includes the construction of an outstanding 1-lane slip road in the original Road T3 Scheme under the Environmental Permit EP-135/2002/J (EP) issued for Schedule 2 Project 'Sha Tin New Town, Stage II - Road T3 and associated roadworks' on 6 February 2014. The construction period of the Contract is tentatively 16 months. The commencement date of major construction works of the Project was scheduled to 19th June 2014.
- 1.3 Cinotech Consultants Limited was commissioned by the CEDD to undertake the Environmental Monitoring and Audit (EM&A) works for the Project.
- 1.4 The site layout plan and the location of noise monitoring station are shown in **Figure 1**.
- 1.5 According to the Baseline Environmental Monitoring Plan submitted to EPD on 21 February 2014, there is one noise monitoring station under the Project for monitoring the impact construction noise. No comment was received from EPD.
- 1.6 This is the 18th monthly EM&A report summarizing the EM&A works conducted for the Projects in November 2015.

Project Organizations

- 1.7 Different parties with different levels of involvement in the project organization include:
 - Project Proponent Civil Engineering and Development Department (CEDD)
 - Engineer's Representative (ER) AECOM
 - Environmental Team (ET) Cinotech Consultants Ltd.
 - Independent Environmental Checker (IEC) ANEWR Consulting Limited
 - Contractor Sheen Billion Development Ltd.
- 1.8 The key contacts of the Project are shown in **Table 1.1**, and the organization chart of ET is shown in **Figure 2**.

Party	Role	Name	Position	Phone No.	Fax No.
CED D	Project	Mr. Bryan YUEN	Engineer	2301 1398	/
CEDD	Proponent	Mr. T.M. KONG	Engineer	2762 5392	2714 5174
AECOM	Engineer's Representative	Mr. Daniel KO	Resident Engineer	2607 7805	2687 2322
Cinotech	Environmental Team Leader	Dr. Priscilla CHOY	Director	2151 2089	3107 1388
ANEWR Independent Checker		Mr. James CHOI	Director	2618 2836	3007 8648
Sheen Billion		Mr. Walance LI	Project Manager	9609 1908	
Development Ltd.	Contractor	Mr. Ryan CHAN	Site Engineer / Environmental Officer	9708 7539	3427 9289

Construction Programme

- 1.9 The site activities undertaken in the reporting month were:
 - Road marking modification
 - Re-surfacing
 - Repaying the cycle-track
 - Drainage and irrigation pipe laying
 - Hydroseeding

Summary of EM&A Requirements

- 1.10 The EM&A programme requires construction phase noise monitoring as well as environmental site audits. The EM&A requirements are described in the following sections, including:
 - All monitoring parameters;
 - Action and Limit levels for all environmental parameters;
 - Event / Action Plans;
 - Environmental mitigation measures, as recommended in the project EIA study final report; and
 - Environmental requirements in contract documents.
- 1.11 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 3 of this report.
- 1.12 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the required monitoring parameters, namely noise as well as audit works for the Project in the reporting month.

2 NOISE MONITORING

Monitoring Requirements

2.1 One noise monitoring station, namely N6 was approved for impact monitoring. **Appendix A** shows the established Action and Limit Level for the environmental monitoring works.

Monitoring Locations

2.2 Noise monitoring was conducted at one designated monitoring station as presented in **Table 2.1**. **Figure 1** shows the location of the monitoring station.

Table 2.1Location of Noise Monitoring Station

Monitoring Station Description		Location of Measurement	
N6	Scenery Court	Block 1 of Scenery Court	

Monitoring Equipment

2.3 **Table 2.2** summarizes the noise monitoring equipment model being used.

Table 2.2Noise Monitoring Equipment

Equipment	Model and Make	Quantity
Integrating Sound Level Meter	SVANTEK - SVAN 955 and SVAN 957	3
Calibrator	SVANTEK - SV30A and B&K - 4231	3

Monitoring Parameters, Frequency and Duration

2.4 **Table 2.3** summarizes the monitoring parameters, frequency and total duration of monitoring.

Table 2.3Noise Monitoring Parameters, Frequency and Duration

Station	Parameter	Period	Frequency	Measurement
N6	$\begin{array}{c} L_{10}(30 \text{ min.}) \ dB(A) \\ L_{90}(30 \text{ min.}) \ dB(A) \\ L_{eq}(30 \text{ min.}) \ dB(A) \\ L_{eq}(5 \text{ min.}) \ dB(A)^* \end{array}$	0700-1900 hrs. on normal weekdays; 1900-2300hrs and 2300-0700 hrs on normal weekdays*	Once a week	Façade

* One set of measurements of impact noise monitoring during the restricted hours (1900-2300hrs and 2300-0700 hrs) were conducted for the night time construction works from 18th to 21st November 2015.

Monitoring Methodology and QA/QC Procedures

Field Monitoring

- 2.5 The monitoring procedures are as follows:
 - The microphone head of the sound level meter was positioned 1m exterior of the noise sensitive facade and lowered sufficiently so that the building's external wall acts as a reflecting surface.
 - The battery condition was checked to ensure good functioning of the meter.
 - Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - frequency weighting : A
 - time weighting : Fast
 - measurement time : 30 minutes
 - Prior to and after noise measurement, the meter was calibrated using the calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement is more than 1.0 dB, the measurement was considered invalid and repeat of noise measurement was required after re-calibration or repair of the equipment.
 - The wind speed at the monitoring station was checked with the portable wind meter. Noise monitoring was cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.
 - Noise measurement was paused during periods of high intrusive noise if possible and observation was recorded when intrusive noise was not avoided.
 - At the end of the monitoring period, the L_{eq} , L_{10} and L_{90} were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.

Maintenance and Calibration

- 2.6 Maintenance and Calibration procedures were as follows:
 - The microphone head of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.
 - The sound level meter and calibrator were checked and calibrated at yearly intervals. Copies of calibration certificates are attached in **Appendix B**.

Results and Observations

- 2.7 In the reporting month, noise monitoring was conducted as scheduled at the designated location. The noise monitoring schedule is provided in **Appendix C**.
- 2.8 All the Construction Noise Levels (CNLs) reported in this report were adjusted with the corresponding baseline level (i.e. Measured Leq Baseline Leq = Measured CNL), in order to facilitate the interpretation of the noise exceedance. The baseline noise level and the allowed CNL at the designated noise monitoring station are presented at Table

2.4.

Table 2.4Baseline Noise Level and Allowed Construction Noise Level for
Monitoring Station

Station	Baseline Noise Level, dB	Allowed CNL, dB (A)
N6 – Scenery Court	66.7	75.0

2.9 The details of the monitoring results and graphical presentations are shown in **Appendix D**. The weather during the monitoring session was sunny and cloudy. In accordance with Condition 6.2 of the EP, all environmental monitoring data was made available to the public via internet access at the website: <u>http://www.st201301.com/test/</u>.

2.10 Two Limit Level exceedances for construction noise monitoring were recorded in the reporting month. The Action/Limit Level and the noise monitoring result are summarized at Table 2.5.

Parameter	Date	CNLs L _{eq} (30min) / L _{eq} (5min)* dB (A)	Action Level	Limit Level
	5 November 2015	68.3		
	13 November 2015	61.9 Measured ≤ Baseline		75dB(A)
	18 November 2015	68.8		
	26 November 2015	62.5	XX 71 1 . 1	
N6	19 November 2015	67.0	When one documented complaint is received	55dB(A)**
		67.2		
		67.1		
		54.5		
	20 November 2015	54.2		40dB(A)**
		53.7		

Table 2.5 Summary Table of Noise Monitoring Results during the Reporting Month

*Three consecutive $L_{eq}(5min)$ were measured for the impact noise monitoring during the restricted hours. **The Project site area falls into Designated Areas, and Prescribed Construction Works would be carried out inside the site boundary during restricted hours. As specified in Technical Memorandum on Noise From Construction Work In Designated Areas, Acceptable Noise Level (ANL) of NSR with Area Sensitivity Rating 'C' for the time period 'All days during the night-time (19:00 to 23:00 hours and 23:00 to 0700 hours) are 55dB(A) and 40dB(A).

2.11 According to our field observations, the major noise sources identified at the designated monitoring station are as follows:

Station	Major Noise Sources
N6 – Scenery Court	Road Traffic

3 ENVIRONMENTAL AUDIT

Site Audits

- 3.1 Site audits were carried out by ET on weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix F**.
- 3.2 Site audits were conducted on 6th, 13th, 20th and 27th November 2015 by ET. A joint site audit with the representative with IEC, ER, the Contractor and the ET was carried out on 27th November 2015. The details of observations during site audit can refer to **Table 3.3**.

Review of Environmental Monitoring Procedures

3.3 The monitoring works conducted by the monitoring team were inspected regularly. The following observations have been recorded for the monitoring works:

Noise Monitoring

- The monitoring team recorded all observations around the monitoring stations, which might affect the monitoring result.
- Major noise sources were identified and recorded. Other intrusive noise attributing to the result was trimmed off by pausing the monitoring temporarily.

Status of Environmental Licensing and Permitting

3.4 All permits/licenses obtained for the Project are summarized in **Table 3.1**.

Permit / License No.	Valid Period		Status			
Fernint / License No.	From	То	Status			
Environmental Permit (EP)	Environmental Permit (EP)					
EP-135/2002/J	6/2/2014	N/A	Valid			
Billing Account for Construction	n Waste Dispo	osal				
RS01172	19/2/2014	N/A	Valid			
Registration of Chemical Waste	e Producer					
WPN5213-758-S3797-01	4/2/2014	12/11/2014	Valid (Updated with two chemical waste types added – spent lubricating oil and			
W110213-730-33797-01	13/11/2014	N/A	contaminated soil with spent lubricating oil)			
Effluent Discharge License under Water Pollution Control Ordinance						
WT00019462-2014	8/7/2014	31/8/2019	Valid			
Construction Noise Permit	Construction Noise Permit					
GW-RN0436-15	5/10/2015	22/112015	Expired			

 Table 3.1
 Summary of Environmental Licensing and Permit Status

Status of Waste Management

3.5 There are 24.01 m³ of Construction and Demolition (C&D) materials generated in this

reporting month. The table summarizing the quantities of waste generated in this reporting month is presented in **Appendix I**.

Implementation Status of Environmental Mitigation Measures

3.6 The key information in the EIA Report is summarized in **Table 3.2**. With referring to the EIA Report, air quality and noise would be the key issues during the construction of the Project. Details of the implementation of mitigation measures are provided in the **Appendix H**.

Table 3.2 Key Information in the EIA Report and the Status of EMIS

	Issues	Assumptions and Assessment	Recommended Mitigation Measures	Status of Implementation of Mitigation Measures
	Air	With the implementation of dust suppression mitigation measures, the level of construction dust would comply with the relevant AQO.	Watering the work area at least twice a day. Environmental pollution control measures for minimizing construction dust impact as stipulated in the APCO.	 During the audit sessions, it was observed that: Watering the work site was provided.
hase	Noise	Noise level at most of NSRs would exceed the noise criteria without mitigation measures.	Good site practices, adoption of quiet construction plant, reduction of on-time operation of plant, movable noise barrier, avoid simultaneous noisy activities.	Duringthe sessions,audit wasobserved that:• Simultaneous activitiesnoisy were avoided.
Construction Phase	Water	The potential impact rose from the construction of flyovers spanning to the upper Shing Mun River Channel.	Construction works spanning the upper Shing Mun River should be undertaken in the dry season All storm runoff should be routed through oil/grit separators and/or sediment basins/traps before being allowed to be discharged into the nearby receiving waters. All stockpiled areas should be covered. All sediment removable facilities should be maintained and the deposited sediments should be removed regularly.	The construction of flyovers spanning to the upper Shing Mun River Channel was completed under Sha Tin New Town – Stage II, Trunk Road T3 Project in 2009

3.7 During site inspections in the reporting month, no non-conformance was identified. The

observations and recommendations made during the audit sessions are summarized in

Parameters	Date	Observations	Remedial Actions
Water Quality	Date 14 August 2015 21 August 2015 28 August 2015 02 September 2015 09 September 2015 16 September 2015 02 October 2015 08 October 2015 16 October 2015 23 October 2015 30 October 2015 13 November 2015 20 November 2015 27 November 2015	Muddy runoff in u-channel should be cleared regularly.	Follow up action will be reported during the next reporting period.
	20 November 2015Unpaved slope should be bundings should be provid27 November 2015Unpaved slope should be bundings should be provid		Follow up action will be reported during the next reporting period.
Air Quality	20 November 2015 27 November 2015	Unpaved slope should be covered and bundings should be provided.	Follow up action will be reported during the next reporting period.
Noise	N/A	N/A	N/A
Waste/ Chemical Management	27 November 2015	Construction waste and general refuse should be removed.	Follow up action will be reported during the next reporting period.
Permit/ Licenses	N/A	N/A	N/A

Table 3.3Observations and Recommendations of Site Audit

Summary of Exceedance

3.8 Two exceedance of monitoring results were recorded in the reporting month. Summary of exceedance is provided in **Appendix E**.

Implementation Status of Event Action Plans

3.9 The Event Action Plan for construction noise is presented in Appendix G. No

exceedance related to the project was recorded and thus no action was required to be implemented.

Summary of Complaint and Prosecution

- 3.10 There was no environmental complaint received in the reporting month.
- 3.11 No prosecution or notification of summons was received in the reporting month. The Complaint Log is attached in **Appendix J.**

4 FUTURE KEY ISSUES

- 4.1 Key issues to be considered in the coming month include:
 - Effluent discharge generated from surface runoff;
 - Dust generation from excavation works, concrete breaking works and stockpile of dusty materials;
 - Noise generation from the operation of PMEs
 - Accumulation of stagnant water in the site areas; and
 - Accumulation of C&D waste on site.

Monitoring Schedule for the Next Month

4.2 The tentative environmental monitoring schedule for the next month is shown in **Appendix C**.

Construction Program for the Next Month

- 4.3 A tentative construction programme is provided in **Appendix K**. The most updated version is provided by Contractor. The major construction activities were ended in August stated in the programme. Some minor construction activities in the coming month will include:
 - Drainage laying
 - Bicycle stands construction
 - Hydroseeding
 - Trees/ shrubs planting

5 CONCLUSIONS AND RECOMMENDATIONS

Conclusions

- 5.1 Environmental monitoring and audit works were conducted in the reporting month. Site inspections were conducted on a weekly basis. The results were reviewed and checked.
- 5.2 All construction noise monitoring was conducted as scheduled in the reporting month. Two Limit Level exceedances were recorded.
- 5.3 There was no environmental complaint received in the reporting month. No prosecution or notification of summons received.

Recommendations

5.4 According to the environmental audit performed in the reporting month, the following recommendations were made:

Water Quality

- Provide mitigation measures to prevent muddy surface runoff from leaking offsite
- Discharge groundwater and surface runoff to the discharge point via sedimentation tank only, and maintain the sedimentation tank to ensure it functions properly


Air Quality


• Regularly clear the sand on haul road and water the haul road to prevent dust generation

Waste / Chemical Management

• Provide mitigation measure to prevent oil spillage/leakage from construction equipment

FIGURE(S)

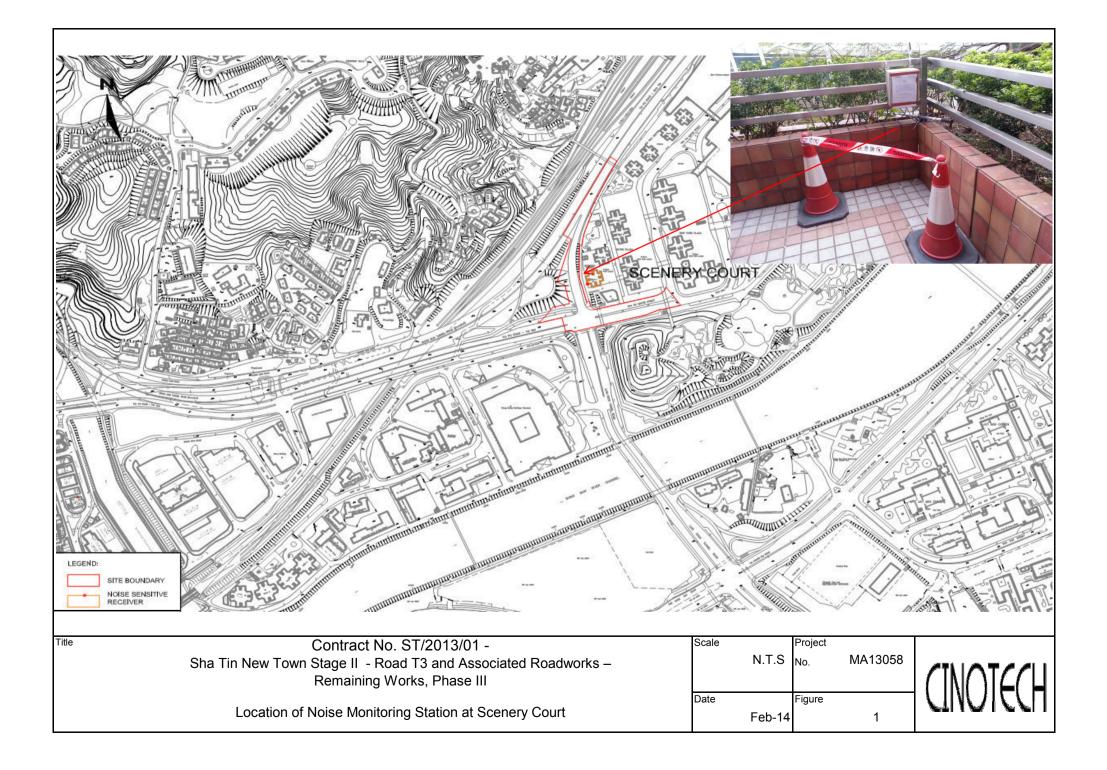

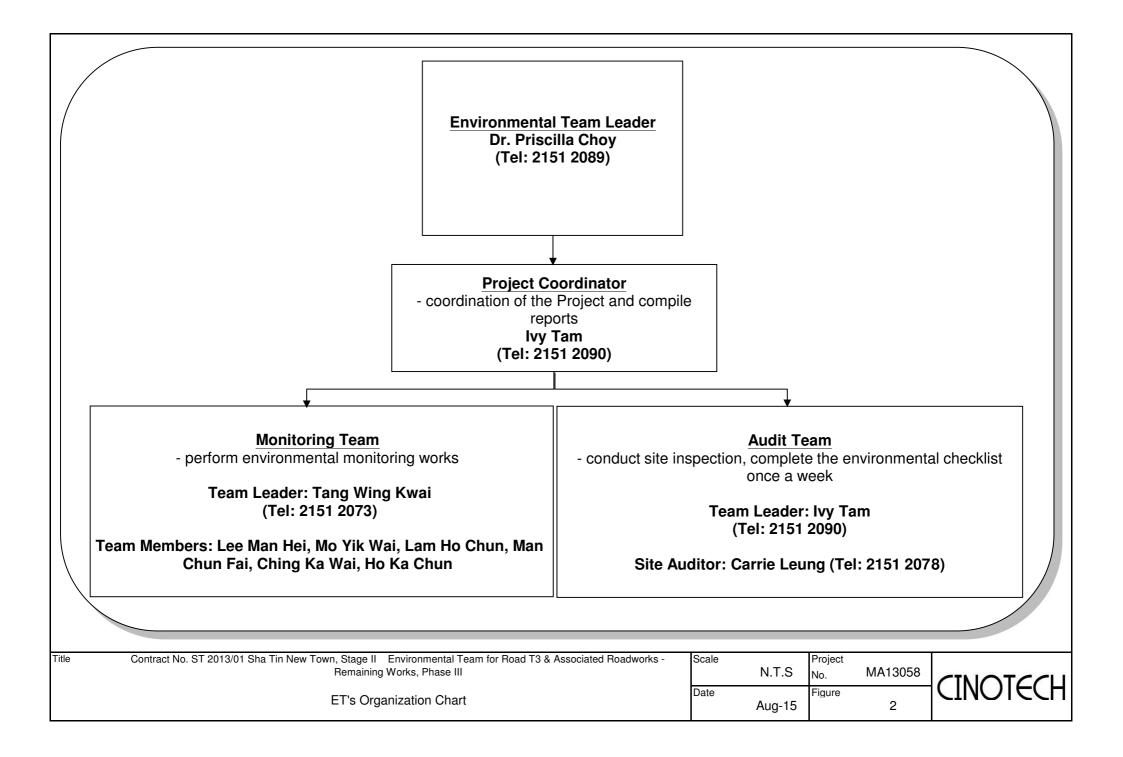

APPENDIX A ACTION AND LIMIT LEVEL

APPENDIX A – Action and Limit Level

Construction Noise

Time Period	Action Level	Limit Level
0700-1900 hrs on normal weekdays		75 dB(A)
0700-2300 hrs on holidays; and 1900- 2300 hrs on all other days	When one documented complaint is received	70* dB(A)
2300-0700 hrs of next day		55* dB(A)

Notes:

Notes: If works are to be carried during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.

(*) reduce to 70 dB(A) for schools and 65 dB(A) during school examination periods.

APPENDIX B COPIES OF CALIBRATION CERTIFCATES



WELLAB LIMITED Rms 816, 1516 & 1701, Technology Park, 18 On Lai Street, Shatin, N.T. Hong Kong. Tel; 2898 7388 Fax: 2898 7076 Website: www.wellab.com.hk

TEST REPORT

APPLICANT: Cinotech Consultants Limited Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong

Test Report No.:	C/N/150103
Date of Issue:	2015-01-05
Date Received:	2015-01-03
Date Tested:	2015-01-03
Date Completed:	2015-01-05
Next Due Date:	2016-01-04
Page:	1 of 1

ATTN:

Mr. W. K. Tang

Certificate of Calibration

Item for calibration:

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 955
Serial No.	: 14303
Microphone No.	: 35222
Equipment No.	: N-08-05
IS:	

Test conditions

Room Temperatre **Relative Humidity** : 20 degree Celsius : 54%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB
94	94.0
. 114	114.0

Remark: 1)This report supersedes the one dated 2012/01/21 with certificate number C/N/120120/1.

PREPARED AND CHECKED BY: For and On Behalf of WELLAB Ltd.

PATRICK TSE Laboratory Manager

This report may not be reproduced except with prior written approval from WELLAB LIMITED and the results relate only to the items calibrated or tested.



WELLAB LIMITED Rms 816, 1516 & 1701, Technology Park, 18 On Lai Street, Shatin, N.T. Hong Kong. Tel: 2898 7388 Fax: 2898 7076 Website: www.wellab.com.hk

TEST REPORT

APPLICANT: Cinotech Consultants Limited Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong

Test Report No.:	C/N/150821/1
Date of Issue:	2015-08-24
Date Received:	2015-08-21
Date Tested:	2015-08-21
Date Completed:	2015-08-24
Next Due Date:	2016-08-23
Page:	1 of 1

ATTN:

Mr. W.K. Tang

Certificate of Calibration

Item for calibration:

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 957
Serial No.	: 21460
Microphone No.	: 43679
Equipment No.	: N-08-09
is:	

Test conditions:

Room Temperatre Relative Humidity : 22 degree Celsius : 54%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

PREPARED AND CHECKED BY: For and On Behalf of WELLAB Ltd.

FATRICK TSE Laboratory Manager



WELLAB LIMITED Rms 816, 1516 & 1701, Technology Park, 18 On Lai Street, Shatin, N.T, Hong Kong. Tel: 2898 7388 Fax: 2898 7076 Website: www.wellab.com.hk

TEST REPORT

APPLICANT: Cinotech Consultants Limited Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong

Test Report No.:	C/N/141129/1_v1
Date of Issue:	2014-12-01
Date Received:	2014-11-29
Date Tested:	2014-11-29
Date Completed:	2014-12-01
Next Due Date:	2015-11-30
Page:	1 of 1

ATTN:

Mr. W.K. Tang

Certificate of Calibration

Item for calibration:

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 957
Serial No.	: 23853
Microphone No.	: 48530
Equipment No.	: N-08-10
15:	

Test conditions:

Room Temperatre Relative Humidity : 20 degree Celsius : 64%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

PREPARED AND CHECKED BY: For and On Behalf of WELLAB Ltd.

PATRICK TSE Laboratory Manager



WELLAB LIMITED Rms 1516, 1701 & 1716, Technology Park, 18 On Lai Street, Shatin, N.T., Hong Kong. Tel: 2898 7388 Fax: 2898 7076 Website: www.wellab.com.hk

Test Report No.: **APPLICANT: Cinotech Consultants Limited** C/N/151031/1 Room 1710, Technology Park, Date of Issue: 2015-11-02 Date Received: 18 On Lai Street, 2015-10-31 Shatin, NT, Hong Kong Date Tested: 2015-10-31 Date Completed: 2015-11-02 Next Due Date: 2016-11-01 ATTN: Page: 1 of 1 Mr. W.K. Tang Item for calibration: Description : Acoustical Calibrator Manufacturer : SVANTEK Model No. : SV30A Serial No. : 10965 : N-09-02 Equipment No. **Test conditions:** Room Temperatre : 24 degree Celsius Relative Humidity : 56%

TEST REPORT

Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

PREPARED AND CHECKED BY: For and On Behalf of WELLAB Ltd.

PATRICK TSE Laboratory Manager



WELLAB LIMITED Rms 816, 1516 & 1701, Technology Park, 18 On Lai Street, Shatin, N.T, Hong Kong. Tel: 2898 7388 Fax: 2898 7076 Website: www.wellab.com.hk

TEST REPORT					
APPLICANT:	Cinotech Consultants L Boom 1710, Technology		Test Report No.:	C/N/151003/1	
	Room 1710, Technology	/ Park,	Date of Issue:	2015-10-04	
	18 On Lai Street,		Date Received:	2015-10-03	
	Shatin, NT, Hong Kong		Date Tested:	2015-10-03	
			Date Completed:	2015-10-04	
			Next Due Date:	2016-10-03	
ATTN:	Mr. W.K. Tang		Page:	1 of 1	
Item for calibra	ation:				
]	Description	: Acoustica	al Calibrator		
J	Manufacturer	: SVANTE	K		
1	Model No.	: SV30A			
ć	Serial No.	: 24803			
I	Equipment No.	: N-09-03			
Test conditions	:				
1	Room Temperatre	: 23 degree	Celsius		
I	Relative Humidity	: 57%			
Methodology:					
	The Sound Level Calibrate locumented procedures and				

recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	$114.0 \pm 0.1 dB$

PREPARED AND CHECKED BY: For and On Behalf of WELLAB Ltd.

(

PATRICK TSE Laboratory Manager

This report may not be reproduced except with prior written approval from WELLAB LIMITED and the results relate only to the items calibrated or tested.



WELLAB LIMITED Rms 816, 1516 & 1701, Technology Park, 18 On Lai Street, Shatin, N.T, Hong Kong. Tel: 2898 7388 Fax: 2898 7076 Website: www.wellab.com.hk

	TEST REPORT					
APPLICANT:			Test Report No.: Date of Issue:	C/N/151003/3 2015-10-04		
	18 On Lai Street,		Date Received:	2015-10-03		
	Shatin, NT, Hong Kong		Date Tested:	2015-10-03		
			Date Completed: Next Due Date:	2015-10-04 2016-10-03		
ATTN:	Mr. W.K. Tang		Page:	1 of 1		
	ation: Description Manufacturer	: Acoustica : SVANTE	al Calibrator			
]	Manufacturer : SVANTE Model No. : SV30A Serial No. : 24791 Equipment No. : N-09-04					
Test conditions	- *					
	Room Temperatre Relative Humidity	: 23 degree : 57%	e Celsius			
Methodology:						

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

PREPARED AND CHECKED BY: For and On Behalf of WELLAB Ltd.

PATRICK TSE Laboratory Manager

This report may not be reproduced except with prior written approval from WELLAB LIMITED and the results relate only to the items calibrated or tested.

APPENDIX C ENVIRONMENTAL MONITORING SCHEDULES

Contract No. ST/2013/01 Sha Tin New Town Stage II Road T3 and Associated Roadworks – Remaining Works, Phase III Noise Monitoring Schedule in November 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Nov	2-Nov	3-Nov	4-Nov	5-Nov	6-Nov	7-Nov
				Noise		
8-Nov	9-Nov	10-Nov	11-Nov	12-Nov	13-Nov	14-Nov
					Noise	
15-Nov	16-Nov	17-Nov	18-Nov	19-Nov	20-Nov	21-Nov
			Noise	Noise*		
22-Nov	23-Nov	24-Nov	25-Nov	26-Nov	27-Nov	28-Nov
				Noise		
29-Nov	30-Nov					

*Night Noise Monitoring conducted during restricted hours (19:00-23:00hrs, 23:00-07:00hrs)

Noise Monitoring Stations

N6 - Scenery Court

Contract No. ST/2013/01 Sha Tin New Town Stage II Road T3 and Associated Roadworks – Remaining Works, Phase III Tentative Noise Monitoring Schedule in December 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-Dec	2-Dec	3-Dec	4-Dec	5-Dec
				Noise		
6-Dec	7-Dec	8-Dec	9-Dec	10-Dec	11-Dec	12-Dec
		Noise				
13-Dec	14-Dec	15-Dec	16-Dec	17-Dec	18-Dec	19-Dec
				Noise		
20-Dec	21-Dec	22-Dec	23-Dec	24-Dec	25-Dec	26-Dec
				Noise		
27-Dec	28-Dec	29-Dec	30-Dec	31-Dec		
The schedule much scheme at				Noise		


The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

*Night Noise Monitoring conducted during restricted hours (19:00-23:00hrs, 23:00-07:00hrs)

APPENDIX D NOISE MONITORING RESULTS AND GRAPHICAL PRESENTATIONS

App D - Noise Monitoring Results

Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
5-Nov-15	9:00	Cloudy	70.6	72.7	67.6	66.7	68.3
13-Nov-15	16:30	Cloudy	61.9	64.2	60.1		61.9 Measured ≤ Baseline
18-Nov-15	10:00	Sunny	70.9	71.5	67.2		68.8
26-Nov-15	17:20	Cloudy	68.1	71.5	65.7		62.5

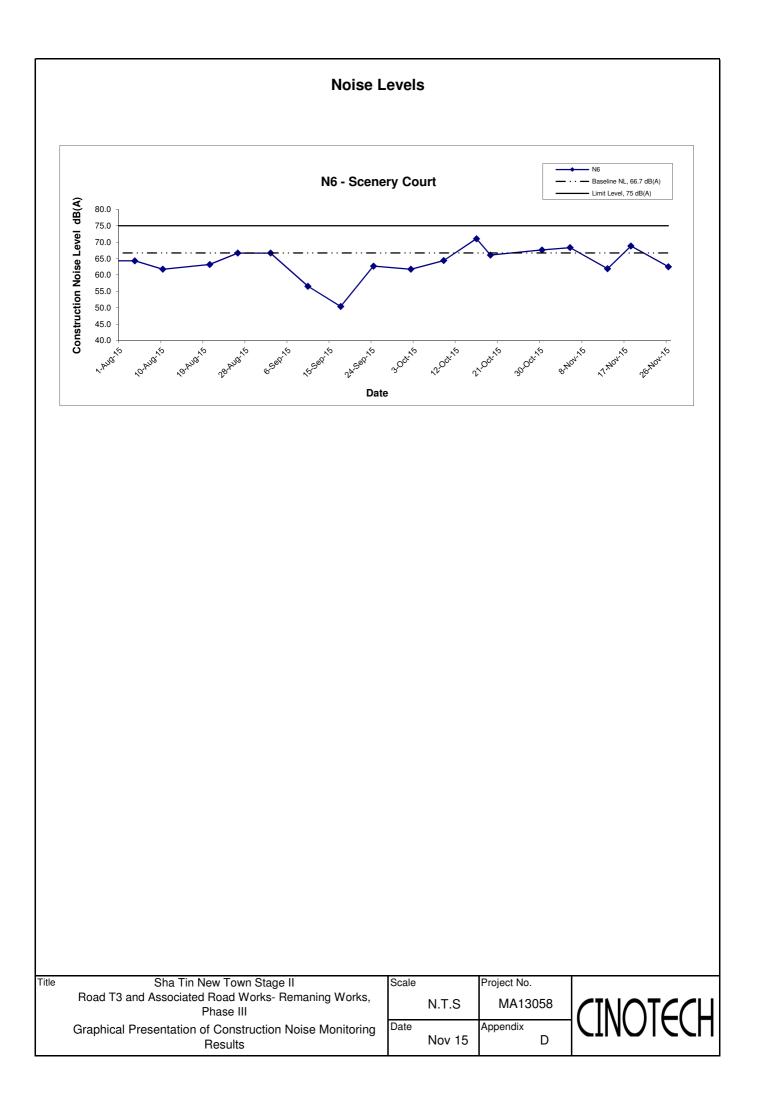

APPENDIX E SUMMARY OF EXCEEDANCE

APPENIDX E – SUMMARY OF EXCEEDANCE

Reporting Month: November 2015

a) Exceedance Report for Construction Noise (NIL)

(Two limit level exceedance were recorded for the impact noise monitoring for the evening and night-time construction works during the restricted hours (17:00-23:00hr and 23:00-0700hr) on 19 and 20 November 2015. The limit level are 55dB(A) (Leq) and 40 dB(A) (Leq) respectively as the Project site area falls into Designated Areas, and Prescribed Construction Works would be carried out inside the site boundary during the restricted hours as per the Technical Memorandum on Noise From Construction Work In Designated Areas)

• Cause of Exceedance:

- Background noise monitoring was conducted before the commencement of works during the restricted hours (19:00-23:00hrs and 23:00-07:00hrs), the major noise source recorded in the background noise measurement was road traffic noise from Tai Po Road and East Rail, and both background noise levels had already exceeded the Limit Levels.
- During construction noise measurement, night works, roadmarking modification was carried out. Traffic noise from Tai Po Road and East Rail was still identified as the major noise source.
- During restricted hours (19:00-23:00hrs) on 19 November 2015, measured noise level was 67.1 dB(A) while the background noise level was 67.4 dB(A) which had already exceeded the Limit level (55 dB(A)).
- During restricted hours (23:00-07:00hrs) on 20 November September 2015, measured noise level was 54.1 dB(A) while the background noise level was 54.3 dB(A) which had already exceeded the Limit level (40 dB(A)).
- With reference to the baseline noise measurement during the restricted hours (19:00-23:00hrs and 23:00-07:00 hrs), the major noise source recorded was road traffic from Tai Po Road and East Rail.
- In view of background noise measurements which was higher than that of impact noise, the exceedance was considered to be contributed from the traffic noise and non-Project related.

• ET's conclusion/recommendations for mitigation:

- The exceedance was considered non-related to the Project works.
- No further mitigation measures would be required.

APPENDIX F SITE AUDIT SUMMARY

Road T3 and Associated Roadworks – Remaining Works, Phase III

Weekly Site Inspection Record Summary

Inspection Information	
Checklist Reference Number	151106
Date	06 November 2015 (Friday)
Time	15:00-16:00

		Related
Ref. No.	Non-Compliance	Item No.
Kel. Ito.	None identified	
	None identified	Related
Ref. No.	Remarks/Observations	Item No.
Kel. INU.	A. Water Quality	
151106-001	Muddy runoff in u-channel should be cleared.	B 8
131100-001	• Muddy function of channel of changes of the	
	B. Air Quality	
	No environmental deficiency was identified during site inspection.	
	C. Noise	
	No environmental deficiency was identified during site inspection.	
	D. Waste/Chemical Management	
	No environmental deficiency was identified during site inspection.	
	E. Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	F. Others	
	 Follow-up on previous site audit session (Ref. No. 151030), follow-up action is required for 	
	the item 151030-001 which was renamed as 151106-001.	<u> </u>

•	Name	Signature	Date
Recorded by	Carrie Leung	Cere	9 November 2015
Checked by	Dr. Priscilla Choy	wh	9 November 2015

Road T3 and Associated Roadworks – Remaining Works, Phase III

Weekly Site Inspection Record Summary

Inspection Information		
Checklist Reference Number	151113	
Date	13 November 2015 (Friday)	
Time	15:00-16:00	

		Related
Ref. No.	Non-Compliance	Item No.
	None identified	
		Related
Ref. No.	Remarks/Observations	Item No.
	A. Water Quality	
151113-R01	Muddy runoff in u-channel should be cleared.	B 8
	B. Air Quality	
	No environmental deficiency was identified during site inspection.	
	C. Noise	
	No environmental deficiency was identified during site inspection.	
	D. Waste/Chemical Management	
	No environmental deficiency was identified during site inspection.	
	E. Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	F. Others	
	• Follow-up on previous site audit session (Ref. No. 151106), follow-up action is required for the item 151106-O01 which was renamed as 151113-R01.	

	Name	Signature	Date
Recorded by	Carrie Leung	Qe	16 November 2015
Checked by	Dr. Priscilla Choy	With	16 November 2015
		1	

Road T3 and Associated Roadworks – Remaining Works, Phase III

Weekly Site Inspection Record Summary

Inspection Information	
Checklist Reference Number	151120
Date	20 November 2015 (Friday)
Time	10:00-11:00

		Related
Ref. No.	Non-Compliance	Item No.
	None identified	=
		Related
Ref. No.	Remarks/Observations	Item No.
	A. Water Quality	
151120-001	Unpaved slope should be covered and bundings should be provided.	B 10
151120-R01	Contractor was reminded to keep cleaning muddy runoff in u-channel.	B 8
	B. Air Quality	
151120-001	Unpaved slope should be covered and bundings should be provided.	C 6
	C. Noise	
	No environmental deficiency was identified during site inspection.	
	D. Waste/Chemical Management	
	No environmental deficiency was identified during site inspection.	
	E. Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	F. Others	
	• Follow-up on previous site audit session (Ref. No. 151113), follow-up action is required for the item 151113-R01 which was renamed as 151120-R01.	

<u>Ca</u> ie	20 November 2015
WIL	20 November 2015
-	Coe W.F

Road T3 and Associated Roadworks – Remaining Works, Phase III

Weekly Site Inspection Record Summary

Inspection Information	
Checklist Reference Number	151127
Date	27 November 2015 (Friday)
Time	10:00-11:30

		Related
Ref. No.	Non-Compliance	Item No.
	None identified	-
		Related
Ref. No.	Remarks/Observations	Item No.
	A. Water Quality	
151127-001	• Unpaved slope should be covered and bundings should be provided.	B 10
151127-R01	Contractor was reminded to keep cleaning muddy runoff in u-channel.	B 8
	B. Air Quality	
151127-001	Unpaved slope should be covered and bundings should be provided.	C 6
	C. Noise	
	No environmental deficiency was identified during site inspection.	
	D. Waste/Chemical Management	-
151127-002	Construction waste and general refuse should be removed.	E li
	E, Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	F. Others	
	• Follow-up on previous site audit session (Ref. No. 151120), follow-up action is required for the item 151120-O01 which was renamed as 151127-O01 and item 151120-R01 which was renamed as 151127-R01.	

	Name	Signature	Date
Recorded by	Carrie Leung	Care	27 November 2015
Checked by	Dr. Priscilla Choy	WR	27 November 2015

1

APPENDIX G EVENT ACTION PLAN

Appendix G Event/Action Plan

Event/Action Plan for Construction Noise

		AC	TION	
EVENT	ET	IEC	ER	CONTRACTOR
ACTION LEVEL	 Undertake measurement to establish validity of complaint Identify the source(s) of the complaint Inform ER & IEC in writing. Discuss remedial actions required with ER & IEC Increase monitoring frequency to assess efficacy of remedial measures 	 Review the analyzed results submitted by the ET Review the proposed remedial measures by the Contractor and advise the ER & ET accordingly Supervise the implementation of remedial measures. 	 Confirm receipt of notification of complaint and notify Contractor if proven Check monitoring data trends and Contractor's working methods. Remind the Contractor of his Contractual obligations and discuss with ET, IEC and Contractor on proposed remedial 	 Submit proposals for remedial actions to ER within three working days of notification Amend proposals if required by the Engineer Implement the remedial actions immediately upon instruction Liaise with the ER to optimise the effectiveness of the agreed mitigation
LIMIT LEVEL	 5. If exceedance continues, meet with ER&IEC to review implementation of appropriate mitigation measures 6. If exceedance stops, cease additional monitoring 		 Contractor on proposed remedial actions. Assess the efficacy of remedial actions and keep the Contractor informed Inform complainant of actions taken 	5. Amend proposal if appropriate
	 Repeat measurement to confirm findings Identify the source(s) of impact Inform ER&IEC and EPD in writing Discuss remedial actions required with ER&IEC Increase monitoring frequency to assess efficacy of remedial measures If exceedance continues, meet with ER&IEC to identify appropriate mitigation measures If exceedance stops, cease additional monitoring 	 Check monitoring data submitted by ET Review Contractor's remedial actions to assure their effectiveness and advise the ER &ET accordingly Supervise the implementation of the remedial measures 	 Confirm receipt of notification of exceedance and notify Contractor Check monitoring data trends and Contractor's working methods Discuss with ET, IC(E) and Contractor on proposed remedial actions to be implemented Assess the efficacy of remedial actions and keep the Contractor informed If exceedance continuous, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is aborted 	 Take immediate action to avoid further exceedance Submit proposals for remedial actions to ER within three working days of notification Amend proposals if required by the ER Implement remedial actions immediately upon instruction Liaise with the ER to optimize the effectiveness of the agreed mitigation Resubmit proposals if problem still not under control Stop the relevant portion of works as determined by the ER until the exceedance is aborted.

APPENDIX H UPDATED ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE

Appendix H - Implementation Schedule of Environmental Mitigation Measures

EIA/ ERR Ref. Ref.	Recommended Mitigation Measures	Who to implement the measures?	Location of the measures	When to Implement the measures?
Construct	tion Noise			-
2.5.4 / 2.3	 Where available, the Contractor shall use quiet items of PME or model of plants that are quieter than those specified in the EPD's Technical Memorandum (GW-TM) for undertaking construction works. Where practicable, the Contractor shall use movable noise barriers and avoid simultaneous noisy activities. 	Contractor	At active construction locations.	Construction stage
Air Qualit	y y			
3.5.3/ 3.4.5	Watering the works area at least twice a day	Contractor	Work site	Construction stage
3.5.4/ 3.4.5	Environmental pollution control measures for minimizing construction dust impact as stipulated in the Air Pollution Control Regulation.	Contractor	Work site	Construction stage
Waste Ma	nagement	·		
5.2 – 5.6/4.5	Environmental pollution control measures for minimizing waste arising from the construction works.	Contractor	Within the works boundary	Construction stage
Water Qua	ality		· · · · ·	
4.5.1/5.5.1	Environmental pollution control measures for minimizing impacts on water quality.	Contractor	All construction sites	Construction stage
Landscap	e and Visual			
-/Table 6-1	Storage of materials and plant shall be limited to areas less visible to receivers.	Contractor	Project site	Construction stage
-/Table 6-1	Preservation wherever possible of existing trees and transplanting wherever practical of trees affected by the Works.	Contractor	Project site	Construction stage
-/Table 6-1	Stripping, storing and re-use of topsoil.	Contractor	Project site	Construction stage

Note: EIA Ref. refers to Trunk Road T3 (Tai Wai) - Updated Final Environmental Impact Assessment Report, March 1998

APPENDIX I WASTE GENERATION IN THE REPORTING MONTH

Civil Engineering and Development Department

Contract No. ST/2013/01 Sha Tin New Town Stage II Road T3 and Associated Roadworks – Remaining Works, Phase III

		A (10 ()			V					(1 N ((11	
		Actual Quanti	ties of Inert C&D	Materials Generate	ed Monthly			Actual Quantities of	C&D wastes G	enerated Monthly	
Month	Total Quantity Generated	Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan	0.366	0.018	0.000	0.000	0.348	0.000	0.000	0.000	0.000	0.000	0.000
Feb	0.218	0.000	0.000	0.000	0.218	0.000	0.000	0.000	0.000	0.000	0.000
Mar	0.318	0.000	0.000	0.000	0.318	0.000	0.000	0.000	0.000	0.000	0.000
Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
May	0.089	0.000	0.000	0.000	0.089	0.000	0.000	0.000	0.000	0.000	0.000
Jun	0.054	0.000	0.000	0.000	0.054	0.000	0.000	0.000	0.000	0.000	0.000
G.Total (Jan-Jun 2015)	1.045	0.018	0.000	0.000	1.027	0.000	0.000	0.000	0.000	0.000	0.000
Jul	0.064	0.038	0.000	0.000	0.026	0.000	0.000	0.000	0.000	0.000	0.000
Aug	0.692	0.000	0.000	0.000	0.692	0.000	0.000	0.000	0.000	0.000	0.000
Sep	0.006	0.000	0.000	0.000	0.006	0.000	0.000	0.000	0.000	0.000	0.000
Oct	0.035	0.000	0.000	0.000	0.035	0.000	0.000	0.000	0.000	0.000	0.000
Nov	0.024	0.000	0.000	0.000	0.024	0.000	0.000	0.000	0.000	0.000	0.000
G.Total	0.821	0.038	0.000	0.000	0.783	0.000	0.000	0.000	0.000	0.000	0.000

Monthly Summary Waste Flow Table for <u>2015</u> (year)

APPENDIX J COMPLAINT LOG

APPENDIX J – COMPLAINT LOG

Reporting Month: November 2015

Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
Com- 2014-11- 01	Tai Po Slip Road	15 th November 2014	The complaint was received from a resident of Hilton Plaza by the Public Relation Officer (PRO) of Contractor (Sheen Billion Development Ltd) at 8:50 a.m. on 15 th November 2014 (Saturday). The complainant concerned about the noisy construction works conducted before 10 a.m.	 According to the information provided by the Contractor, the noisy construction work at the time of complaint was concrete breaking work using an excavator-mounted breaker. No violation of the Noise Control Ordinance as the noisy construction work was conducted within the non-restricted hour (07:00 to 19:00 on normal weekdays). However, according to item 2 of section 25.11B in PS of the Contract, demolition of existing artificial hard material should not be conducted during 8a.m. to 10a.m. Thus, the Contractor did not fulfil such requirement. After received the complaint, PRO coordinated the site personnel to stop the noisy works once the complaint was received. The noisy construction works have been re-scheduled to be commenced after 10 a.m. based on the requirement specified in the PS. 	Closed
Com- 2014-12- 01	Tai Po Slip Road	29 th December 2014	The complaint was received by Environmental Protection Department (EPD) (EPD Complaint Ref: RN32146-14) in the morning of 29 th December 2014. The complainant complained about the effluent discharge to a gully in the worksite may cause pollution to the nearby environment.	According to the information provided by the Contractor, the effluent discharge was due to groundwater leakage from the trench excavation at deep depth of Bay 7 of the worksite. Since site inspection was also conducted in the morning of 29 th December 2014 and no improper effluent discharge was observed, it is likely that the complainant observed the issue before 29 th December 2014.	Closed

Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
				Improper effluent discharge was observed during the site inspections on 3 rd , 10 th and 22 nd December 2014. Recommendations were given to the Contractor during the site inspections, and a further reminder was also given to the Contractor through email dated 22 nd December 2014.	
				The improper effluent discharge was ceased as per the rectified photos given by the Contractor on 24 th December 2014, as well as during the site inspection on 6 th January 2015. The discharge pipes were also connected to the discharge point via the sediment tank as per the photographic records given by the Contractor on 6 th January 2015 and from the site inspection on 7 th January 2015.	

APPENDIX K CONSTRUCTION PROGRAMME

					2014 2015 2016
	Task Name Whole of the works	Duration 878.5 days	Start Tue 28/1/14	Finish Fri 24/6/16	Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan
2		010.0 00.9	100 200 1014	1112-0010	
	Preliminaries	105.1	E . 0011114	N. 100/60.6	
3	RE office take-over	485 days	Tue 28/1/14	Wed 27/5/15	
		28 days	Tue 28/1/14	Mon 24/2/14	
	Site Office set up	90 days	Tue 28/1/14	Sun 27/4/14	
	Site setting-out & project signboard erection	35 days	Tue 28/1/14	Mon 3/3/14	
	Public Relation Plan	485 days	Tue 28/1/14	Wed 27/5/15	
	Plan Preparation and submission for approval	75 days	Tue 28/1/14	Sat 12/4/14	
	Preparation for 1st CLG meeting	10 days	Sun 13/4/14	Tue 22/4/14	
,	Plan implementation	400 days	Wed 23/4/14	Wed 27/5/15	
	Material & Method Statement submission	120 days	Tue 28/1/14	Tue 27/5/14	
	Noise Barrier System submission	64 days	Sat 15/3/14	Sat 17/5/14	
	Preparation for material submission and approval	15 days	Sat 15/3/14	Sat 29/3/14	
-	Preparation for shop drawing & design calculation submission and approval	42 days	Sun 30/3/14	Sat 10/5/14	
-	Design and Check Certificate provision	7 days	Sun 11/5/14	Sat 17/5/14	
-		, days	5011 11/5/14	5at 17/J/14	
_	Section I Works - Noise barrier & roadworks	500 days	T 0014144		
-		526 days	Tue 28/1/14	Tue 7/7/15	
	TTA preparation	60 days	Tue 28/1/14	Fri 28/3/14	
	TTA submission and approval and Gazzette publication	67 days	Sat 29/3/14	Tue 3/6/14	
	CCTV inspection of existing drains/sewer and report submission	30 days	Mon 19/5/14	Tue 17/6/14	
7	Preparation works for T3 slip road closure on 8Jun 2014	12 days	Wed 4/6/14	Sun 15/6/14	
1	RA application	5 days	Wed 4/6/14	Sun 8/6/14	
1	Permemant / temp. gantry sign plates replacement	5 days	Wed 4/6/14	Sun 8/6/14	
1	Permenant / temp. traffic signs provision	7 days	Mon 9/6/14	Sun 15/6/14	
-	TTA set up for slip road lane closure	1 day	Sun 8/6/14	Sun 8/6/14	
-	1st stage modification of traffic signal at J/O Sha Tin Centre St & Lion Rock Tunnel Rd	1 day	Sun 8/6/14	Sun 8/6/14	
-	Road marking modification works	l day	Sun 8/6/14	Sun 8/6/14	
-	Sit setting out works	3 days	Mon 9/6/14	Wed 11/6/14	
-	UU detection and trialpit excavation				
-	UU diversion	2 days	Thu 12/6/14	Fri 13/6/14	
-		7 days	Sat 14/6/14	Fri 20/6/14	
_	Joint site inspection with LCSD for site pocession at LCSD area & record taking	7 days	Mon 16/6/14	Sun 22/6/14	
	Site setup, Signboard and hoarding erection	14 days	Sat 14/6/14	Fri 27/6/14	
	Modification works to existing traffic sign plates and posts	353 days	Mon 9/6/14	Wed 27/5/15	
	TTA submission & RA application	73 days	Mon 9/6/14	Wed 20/8/14	
1	TDS 1	35 days	Thu 21/8/14	Wed 24/9/14	<u>₹</u>
1	NTE/ST/SHATINRC-05	35 days	Thu 25/9/14	Wed 29/10/14	
1	NTE/ST/TAIPO-37	35 days	Thu 30/10/14	Wed 3/12/14	
1	NTE/ST/SHATINRC-06	35 days	Thu 4/12/14	Wed 7/1/15	
1	NTE/ST/SHATINRC-03	35 days	Thu 8/1/15	Wed 11/2/15	
-	NTE/ST/SHATINRC-01B	35 days	Thu 12/2/15	Wed 18/3/15	
1					

	rogram No.7 for Contract ST/2013/01			
ID	Tarl. Mana	Duri	Ctor 1	D:-: 1
ID T 42	Task Name NTE/ST/MANLAM-01A	Duration 35 days	Start Thu 23/4/15	Finish Wed 27/5/15
43	Site clearance and street furniture removal at slip road	7 days	Thu 12/6/14	Wed 18/6/14
44	Noise barrier (NB) construction	416 days	Sun 18/5/14	Tue 7/7/15
45	Material procument and panel delivery	180 days	Sun 18/5/14	Thu 13/11/14
46	Breakup & dispose of extg hard material	5 days	Thu 19/6/14	Mon 23/6/14
47	EOT granted due to Inclement Weather in Jul. & Aug14 (EOT Order No. 2 & 3)	19.5 days	Tue 24/6/14	Sun 13/7/14
48	Tentative EOT Claims due to Claim No.4	10 days	Sun 13/7/14	Wed 23/7/14
49	Tentative EOT claim due to Inclement Weather in Sep.14	9 days	Wed 23/7/14	Fri 1/8/14
50	Bay 1 & 2 (1st Portion) Footing construction	81.5 days	Fri 1/8/14	Tue 21/10/14
51	Bay 1 Footing Construction	76 days	Fri 1/8/14	Thu 16/10/14
52	ELS system installation & surplus material disposal	40 days	Fri 1/8/14	Wed 10/9/14
	Forwork erection & steel reinforcement fixing	-	Wed 10/9/14	Sat 4/10/14
53		24 days		a summer
54	Concreting & curing	7 days	Sat 4/10/14	Sat 11/10/14
55	Formwork removal & soil backfill	5 days	Sat 11/10/14	Thu 16/10/14
56	Bay 2 Footing Construction (1st portion of 5m length)	46 days	Mon 1/9/14	Thu 16/10/14
57	ELS system installation & surplus material disposal	14 days	Mon 1/9/14	Sun 14/9/14
58	Tentative EOTclaims due to conflict with unexpected watermains	7 days	Mon 15/9/14	Sun 21/9/14
59	Forwork erection & steel reinforcement fixing for base slab	5 days	Mon 22/9/14	Fri 26/9/14
60	Concreting	l day	Sat 27/9/14	Sat 27/9/14
51	Forwork erection & steel reinforcement fixing for wall stem	7 days	Sun 28/9/14	Sat 4/10/14
52	Concreting & curing	7 days	Sun 5/10/14	Sat 11/10/14
53	Formwork removal & soil backfill	5 days	Sun 12/10/14	Thu 16/10/14
54	ELS system removal	5 days	Fri 17/10/14	Tue 21/10/14
55	Existing boundary wall (Bay 2 ~ Bay 5) demolition	50 days	Sun 12/10/14	Sun 30/11/14
6	Temporary access reprovision	7 days	Sun 12/10/14	Sat 18/10/14
57	Break up and dispose of extg boundary wall along Bay 5 & wall stem along Bay 4 ~ Bay2	16 days	Sun 19/10/14	Mon 3/11/14
18	Break up and dispose of extg boundary wall (footing) along Bay 4	9 days	Tue 4/11/14	Wed 12/11/14
19	Break up and dispose of extg boundary wall (footing) along Bay 3	9 days	Thu 13/11/14	Fri 21/11/14
	Break up and dispose of extg boundary wall (footing) along Bay 2	9 days	Sat 22/11/14	Sun 30/11/14
0		mant management		
1	Bay 6 & 7 Footing construction	128 days	Mon 22/9/14	Tue 27/1/15
2	Access setup, locate extg UU & breakup extg boundary wall	28 days	Mon 22/9/14	Sun 19/10/14
3	Shoring installation along Bays without UU disturbance (I.e. Bay 3-5 & portion of Bay 6&7)	12 days	Mon 20/10/14	Fri 31/10/14
4	Tentative EOT Claims due to extg. Sheet-pile, WSD pipe & PCCW cable ducts	28 days	Sat 1/11/14	Fri 28/11/14
5	Bay 7 Construction	38 days	Sat 29/11/14	Mon 5/1/15
5	ELS system installation & surplus material disposal	14 days	Sat 29/11/14	Fri 12/12/14
7	Forwork erection & steel reinforcement fixing	14 days	Sat 13/12/14	Fri 26/12/14
3	Concreting & curing	10 days	Sat 27/12/14	Mon 5/1/15
)	Bay 6 construction	34 days	Sat 13/12/14	Thu 15/1/15
)	Excavation & surplus material disposal	10 days	Sat 13/12/14	Mon 22/12/14
	Forwork erection & steel reinforcement fixing	14 days	Tue 23/12/14	Mon 5/1/15
2	Concreting & curing	10 days	Tue 6/1/15	Thu 15/1/15

ID	Task Name	Duration	Start	Disish	2015 an Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov
3	Task IName Formwork removal & soil backfill	Duration 7 days	Start Fri 16/1/15	Finish Thu 22/1/15	an reb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan reb Mar Apr May Jun Jul Aug Sep Oct Nov
4	ELS system removal	5 days	Fri 23/1/15	Tue 27/1/15	
5	Bay 4 & 5 Footing construction	52 days	Fri 23/1/15	Sun 15/3/15	
_	Excavation & surplus material disposal	12 days	Fri 23/1/15	Tue 3/2/15	
1	Forwork erection & steel reinforcement fixing	18 days	Wed 4/2/15	Sat 21/2/15	
-	Concreting & curing	10 days	Sun 22/2/15	Tue 3/3/15	
-	Formwork removal & soil backfill	7 days	Wed 4/3/15	Tue 10/3/15	
1	ELS system removal	5 days	Wed 11/3/15	Sun 15/3/15	
1	Bay 3 and 2 (2nd portion of 7m span) Footing construction	52 days	Mon 16/3/15	Wed 6/5/15	
1	Excavation & surplus material disposal	12 days	Mon 16/3/15	Fri 27/3/15	
1	Forwork erection & steel reinforcement fixing	18 days	Sat 28/3/15	Tue 14/4/15	
1	Concreting & curing	10 days	Wed 15/4/15	Fri 24/4/15	
1	Formwork removal & soil backfill	7 days	Sat 25/4/15	Fri 1/5/15	
	ELS system removal	5 days	Sat 2/5/15	Wed 6/5/15	
	Noise Barrier Sytem Steelwork Erection	140 days	Wed 28/1/15	Tue 16/6/15	
	Noise Barrier Panel, cladding and gutter fixing	21 days	Wed 17/6/15	Tue 7/7/15	
-	New Sign Gantry construction	283 days	Mon 1/9/14	Wed 10/6/15	
	Shop drawing and E&M works submission and approval	150 days	Mon 1/9/14	Wed 28/1/15	
-	Footing modification	21 days	Thu 7/5/15	Wed 27/5/15	
1	Steelwork fabrication, delivery & erection	14 days	Thu 28/5/15	Wed 10/6/15	
	Drainage works	28 days	Thu 7/5/15	Wed 3/6/15	
1	Carriageway construction	34 days	Thu 4/6/15	Tue 7/7/15	
1	St lighting duct laying and street furniture provision	12 days	Thu 11/6/15	Mon 22/6/15	Г <mark>Т</mark>
1	Irrigation system construction	7 days	Tue 23/6/15	Mon 29/6/15	
	Cycletracks & footpath construction	14 days	Tue 23/6/15	Mon 6/7/15	
-	Landscaping works	27 days	Thu 11/6/15	Tue 7/7/15	
-	2nd stage modification of traffic signal at J/O Sha Tin Centre St & Lion Rock Tunnel Rd	1 day	Tue 7/7/15	Tue 7/7/15	
,	Joint site inspection with LCSD for handover posessed site	l day	Tue 7/7/15	Tue 7/7/15	
		····· ·· · · · · · · · · · · · · · · ·			

Page 3
