



AUES PROJECT NO. TCS/00704/14

CONTRACT NO. MTRC6593-13C –
WAN CHAI STATION LEE TUNG STREET SUBWAY

1ST ENVIRONMENTAL MONITORING AND AUDIT
(EM&A) MONTHLY REPORT – SEPTEMBER 2014

PREPARED FOR
KADEN CONSTRUCTION LIMITED

Quality Index

| Date | Reference No. | Prepared By | Approved By |
|-----------------|-------------------------|--|---|
| 16 October 2014 | TCS00704/14/600/R0021v2 |  Nicola Hon Environmental Consultant |  T.W. Tam Environmental Team Leader |

| Version | Date | Description |
|---------|-----------------|---|
| 1 | 7 October 2014 | First Submission |
| 2 | 16 October 2014 | Amended against the IEC's comment on 9 October 2014 |
| | | |



16 October 2014

By Email and Poste

MTR Corporation Limited
Fo Tan Railway House
No. 9, Lok King Street, Fo Tan
Shatin, N.T., Hong Kong

Your reference:

Our reference: 40032976/432914

Attention: Mr. Kenneth Chow / Environmental
Engineer II

Dear Sir,

**Consultancy Agreement A130-13
Independent Environmental Checker for CRS and LTS
LTS - Verification for First Monthly Environmental Monitoring and Audit (EM&A) Report
(September 2014) (Report No.: TCS00704/14/600/R0021v2)**

We refer to the First Monthly EM&A Report (September 2014) received under cover of the email from the Environmental Team, AUES, dated on 9 October 2014.

Further to our comments provided on 9 October 2014 and subsequent revision of the Report by AUES on 16 October 2014, we have no comment and have verified the captioned report (Report No.: TCS00704/14/600/R0021v2).

Should you have any queries, please feel free to contact the undersigned at 2410 3795.

Yours faithfully
URS Hong Kong Ltd

Thomas Wong
Deputy Independent Environmental Checker

TWKW/wwsc

cc. via email
Kaden Construction Limited (Attn.: Mr. Ronald Fung)
AUES (Attn.: Ms. Nicola Hon)

URS Hong Kong Ltd
優斯(香港)有限公司
38th Floor, Metroplaza Tower 1
223 Hing Fong Road, Kwai Fong, Hong Kong
Tel: +852 2428 8866 Fax: +852 2428 9922
email: hk.info@urs.com
www.urs.com

商界展關懷
caringcompany
Awarded by The Hong Kong Council of Social Service
香港社會服務發展局



ISO 9001 : 2008
Certificate No.: CC 213

EXECUTIVE SUMMARY

- ES01 **KADEN CONSTRUCTION LIMITED** (hereinafter ‘KCL’) has been awarded by the MTR Corporation Limited (MTRCL) of the Contract No. *MTRC6593-13C – Wan Chai Station Lee Tung Street Subway* (hereinafter “the Project”), which is a Designated Project to be implemented under Environmental Permit EP-444/2012/A (hereinafter referred as “the EP-444/2012/A” or “the EP”). The Project Profile has been approved under the Environmental Impact Assessment Ordinance (EIAO).
- ES02 The Project includes redevelopment of the Lee Tung Street area to improve pedestrian networking by enhancing the accessibility, connectivity and circulation of human traffic north-south from Queen’s Road East area to Wan Chai MTR Station, and providing a safe and attractive means for pedestrian crossing of Johnston Road. The Project is expected to take about 36 months.
- ES03 Action-United Environmental Services & Consulting (hereinafter referred as “AUES”) has been commissioned as the Environmental Team for the Project (hereinafter referred as “the ET”) to perform relevant EM&A programme in accordance with the Environmental Monitoring and Audit Plan (EMAP) which enclosed in the Project Profile.
- ES04 According to the Approved EMAP, air quality and noise monitoring are required to be monitored during construction of the Project. Pursuant to the EP, baseline environmental monitoring is required to conduct prior to commencement of construction works under the Project. So baseline monitoring of air quality was undertaken in period from **3 June 2014** to **16 June 2014**; moreover continuous noise measurement was carried out between **4 June 2014** and **19 June 2014**. Furthermore, the Baseline Monitoring Report which verified by the Independent Environmental Checker (hereinafter referred as “the IEC”) has been submitted to Environmental Protection Department (EPD) on **15 July 2014** for endorsement.
- ES05 According to **Section 3.3** of the EP, the Baseline Monitoring Report shall be deposited to EPD at least two weeks before commencement of the construction of the Project. The construction of the Project as well as the EM&A Programme in relevant section was therefore commenced on **28 August 2014** to comply with the EP and EMAP requirements.
- ES06 This is the **1st** monthly EM&A report presenting the monitoring results and inspection findings for the reporting period from **28 August 2014** to **30 September 2014** (hereinafter ‘the Reporting Period’).

SUMMARY OF ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

- ES07 The monitoring and audit activities during the Reporting Period are summarized in below:-

| Environmental Aspect | Environmental Monitoring Parameters / Inspection | Reporting Period | |
|----------------------|--|-------------------------------|-----------------|
| | | Number of Monitoring Location | Total Occasions |
| Air Quality | 24-hour TSP | 1 | 7 |
| Construction Noise | L _{eq(30min)} Daytime | 2 | 10 |
| Site Inspection / | Joint with ET, the Contractor and RE | -- | 5 |
| Audit | Joint with IEC, ET, the Contractor and RE | -- | 1 |

BREACH OF ACTION AND LIMIT (A/L) LEVELS

- ES08 In the Reporting Period, no air quality exceedance was registered. Moreover, no noise complaint (i.e. Action Level) was received. However, three occasions of noise measurement result higher than 75dB(A) were recorded at N2 (balcony at 1/F of Chiu Hin Mansion). As reviewed the baseline noise monitoring data of N2, high background noise is already exist. In order to find the actual construction noise, the exceeded noise measurement results were adjusted by the baseline monitoring data. After adjustment, the construction noise levels of the Project were

indicated below 75dB(A). No Notifications of Exceedances (NOEs) therefore was issued to the RE, IEC and the Main Contractor. The statistics of environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

| Environmental Aspect | Monitoring Parameters | Action Level | Limit Level | Event & Action | | |
|----------------------|-------------------------|--------------|-------------|----------------|---------------|--------------------|
| | | | | NOE Issued | Investigation | Corrective Actions |
| Air Quality | 24-hour TSP | 0 | 0 | 0 | 0 | 0 |
| Construction Noise | $L_{eq(30min)}$ Daytime | 0 | 0 | 0 | 0 | 0 |

ENVIRONMENTAL COMPLAINT

ES09 No public complaints were received by either the EPD or MTRCL or the Main Contractor in the Reporting Period.

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES010 No environmental summons or successful prosecutions were recorded in the Reporting Period.

REPORTING CHANGE

ES011 As this is the first Monthly EM&A Report, no reporting changes were made in the Reporting Period.

SITE INSPECTION

ES012 In the Reporting Period, weekly site inspection by the MTRC and ET and Main Contractor has been carried out on **28 August, 4, 11, 18, 25** and **29 September 2014** and the IEC was joined the site inspection **11 September 2014**. No non-compliance observed during the site inspection. Furthermore, no site inspection was undertaken by external parties i.e. EPD and AFCD in this Reporting Month.

FUTURE KEY ISSUES

ES013 Construction noise would be a key environmental issue during construction work of the Project. Noise mitigation measures should be implemented in accordance with the EMAP requirement.

ES014 Moreover, special attention should be paid on the potential construction dust impact since the construction site is located on an urban area. The Contractor should fully implement the construction dust mitigation measures properly.

ES015 In addition, the potential water quality impact at the nearby public areas should be highly alerted especially during rainy season from April to October. The Contractor should prevent muddy water and other water pollutants via site surface water runoff get into public areas, water quality mitigation measures should be properly implemented.

TABLE OF CONTENTS

| | | |
|----------|---|-----------|
| 1 | INTRODUCTION | 1 |
| | PROJECT BACKGROUND | 1 |
| | REPORT STRUCTURE | 1 |
| 2 | PROJECT ORGANIZATION AND SUBMISSION | 2 |
| | PROJECT ORGANIZATION | 2 |
| | SUMMARY OF ENVIRONMENTAL SUBMISSIONS | 3 |
| 3 | ENVIRONMENTAL IMPACT MONITORING REQUIREMENT | 5 |
| | MONITORING PARAMETERS | 5 |
| | MONITORING LOCATIONS | 5 |
| | MONITORING FREQUENCY AND PERIOD | 5 |
| | MONITORING EQUIPMENT | 6 |
| | MONITORING METHODOLOGY | 7 |
| | DERIVATION OF ACTION/LIMIT (A/L) LEVELS | 8 |
| | DATA MANAGEMENT AND DATA QA/QC CONTROL | 8 |
| 4 | MONITORING RESULTS | 9 |
| | 24-HOUR TSP AIR QUALITY MONITORING RESULTS | 9 |
| | NOISE MONITORING RESULTS | 9 |
| 5 | WASTE MANAGEMENT | 11 |
| | GENERAL WASTE MANAGEMENT | 11 |
| | RECORDS OF WASTE QUANTITIES | 11 |
| 6 | SITE INSPECTION | 12 |
| | FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH | 12 |
| 7 | ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE | 13 |
| | ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION | 13 |
| 8 | IMPLEMENTATION STATUS OF MITIGATION MEASURES | 14 |
| | GENERAL REQUIREMENTS | 14 |
| | KEY ISSUES FOR THE COMING MONTH | 15 |
| 9 | CONCLUSIONS AND RECOMMENDATIONS | 16 |
| | CONCLUSION | 16 |
| | RECOMMENDATIONS | 16 |

LIST OF TABLES

| | |
|-----------|--|
| TABLE 2-1 | SUBMISSION/SET-UP STATUS OF THE EP REQUIREMENTS |
| TABLE 2-2 | STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACTS |
| TABLE 3-1 | SUMMARY OF THE MONITORING PARAMETERS OF EM&A REQUIREMENTS |
| TABLE 3-2 | AIR AND NOISE MONITORING LOCATIONS |
| TABLE 3-3 | AIR QUALITY MONITORING EQUIPMENT |
| TABLE 3-4 | CONSTRUCTION NOISE MONITORING EQUIPMENT |
| TABLE 3-5 | ACTION AND LIMIT LEVELS FOR AIR QUALITY MONITORING |
| TABLE 3-6 | ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE |
| TABLE 4-1 | SUMMARY OF 24-HOUR TSP MONITORING RESULTS – A1 |
| TABLE 4-2 | NOISE MONITORING RESULTS OF N1 (2/F FLOOR OF HENNESSEY BUILDING), (dB(A)) |
| TABLE 4-3 | NOISE MONITORING RESULTS OF N2 (BALCONY AT 1/F OF CHIU HIN MANSION), (dB(A)) |
| TABLE 4-4 | ADJUSTMENT OF CONSTRUCTION NOISE LEVEL FOR N2, dB(A) |
| TABLE 5-1 | SUMMARY OF QUANTITIES OF INERT C&D MATERIALS |
| TABLE 5-2 | SUMMARY OF QUANTITIES OF C&D WASTES |

| | |
|-----------|--|
| TABLE 6-1 | SITE OBSERVATIONS |
| TABLE 7-1 | STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS |
| TABLE 7-2 | STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS |
| TABLE 7-3 | STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION |
| TABLE 8-1 | ENVIRONMENTAL MITIGATION MEASURES |

LIST OF APPENDICES

| | |
|------------|---|
| APPENDIX A | PROJECT SITE LAYOUT PLAN |
| APPENDIX B | ORGANIZATION OF THE PROJECT AND MASTER CONSTRUCTION PROGRAMME |
| APPENDIX C | MONITORING LOCATIONS |
| APPENDIX D | CALIBRATION CERTIFICATE OF MONITORING EQUIPMENT |
| APPENDIX E | HOKLAS-ACCREDITATION CERTIFICATE OF THE TESTING LABORATORY |
| APPENDIX F | EVENT AND ACTION PLAN |
| APPENDIX G | MONITORING SCHEDULE |
| APPENDIX H | DATABASE OF MONITORING RESULTS |
| APPENDIX I | GRAPHICAL PLOTS |
| APPENDIX J | METEOROLOGICAL INFORMATION |
| APPENDIX K | MONTHLY SUMMARY WASTE FLOW TABLE |
| APPENDIX L | IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM) |

1 INTRODUCTION

PROJECT BACKGROUND

- 1.01 **KADEN CONSTRUCTION LIMITED** (hereinafter ‘KCL’) has been awarded by the MTR Corporation Limited (MTRCL) of the Contract No. *MTRC6593-13C – Wan Chai Station Lee Tung Street Subway* (hereinafter “the Project”), which is a Designated Project to be implemented under Environmental Permit EP-444/2012 (hereinafter referred as “the EP-444/2012” or “the EP”).
- 1.02 The Project includes redevelopment of the Lee Tung Street area to improve pedestrian networking by enhancing the accessibility, connectivity and circulation of human traffic north-south from Queen’s Road East area to Wan Chai MTR Station, and providing a safe and attractive means for pedestrian crossing of Johnston Road. The Project site layout plan is shown in [Appendix A](#) and works under the Project comprise:
- (i) Construction of a pedestrian subway link between Urban Renewal Authority’s Redevelopment at Site H15 (the Development) and Wan Chai Station (WAC);
 - (ii) Construction of two ventilation shafts; and
 - (iii) Modification works of some of the station concourse.
- 1.03 The Project is expected to take about 36 months. In order to effectively implement the environmental protection measures as stipulated in the Particular Specification (PS) of Project, an Environmental Monitoring and Audit Plan (EMAP) which enclosed in the Project Profile (PP) was prepared to guide the setup of the environmental monitoring and audit (EM&A) programme of the Project.
- 1.04 Action-United Environmental Services and Consulting (AUES) has been commissioned by KCL as the independent environmental team (ET) to implement the relevant EM&A programme of the Project.
- 1.05 The baseline monitoring program was carried out during the period between **3 June 2014** and **19 June 2014** at the proposed monitoring locations by the ET according to the approved EMAP. The “Baseline Monitoring Report (R0010 Version 4)” which has verified by IEC, was submitted to EPD on **15 July 2014** before commencement of major construction works. As notified by KCL, the construction of the Project was commenced on 28 August 2014. Therefore, EM&A programme was started on 28 August 2014.
- 1.06 This is **1st** monthly EM&A report presenting the monitoring results and inspection findings in The Reporting Period from **28 August** to **30 September 2014**.

REPORT STRUCTURE

- 1.07 This Report is structured into the following sections:-
- Section 1 Introduction*
 - Section 2 Project Organization*
 - Section 3 Environmental Impact Monitoring Requirement*
 - Section 4 Monitoring Results*
 - Section 5 Waste Management*
 - Section 6 Site Inspections*
 - Section 7 Environmental Complaint and Non-Compliance*
 - Section 8 Implementation Status of Mitigation Measures*
 - Section 9 Conclusions and Recommendations*

2 PROJECT ORGANIZATION AND SUBMISSION

PROJECT ORGANIZATION

2.01 The project organization is shown in [Appendix B](#). The responsibilities of respective parties are:

MTR Corporation Limited (MTRCL)

2.02 MTRCL is the Project Proponent and the Permit Holder of the EP of the development of the Project and will assume overall responsibility for the project. Also, an Independent Environmental Checker (IEC) should be employed by MTRCL to audit the results of the EM&A work conducted by Environmental Team.

Environmental Protection Department (EPD)

2.03 EPD is the statutory enforcement body for environmental protection matters in Hong Kong.

Resident Engineer (RE)

2.04 The RE is responsible for overseeing the construction works and for ensuring that the works are undertaken by the Contractor in accordance with the specification and contract requirements. The duties and responsibilities of the ER with respect to EM&A are:

- Monitor the Contractor's compliance with Contract Specifications, including the effective implementation and operation of the environmental mitigation measures;
- Inform the Contractor when action is required to reduce impacts in accordance with the Event and Action Plans;
- Participate in site inspections undertaken by the ET; and
- Co-operate with the ET in providing all the necessary information and assistance for completion of the complaint investigation works.

Independent Environmental Checker (IEC)

2.05 The IEC should advise the ET and RE on environmental issues related to the project. The IEC should audit from an independent viewpoint on the environmental performance during the construction of the project. The IEC should be a person who has relevant professional qualifications in environmental control and at least 7 years' experience in EM&A and environmental management. The duties and responsibilities of the IEC are:

- Review and audit in an independent, objective and professional manner in all aspects of the EM&A programme;
- Validate and confirm the accuracy of monitoring results, appropriateness of monitoring equipment, monitoring locations with reference to the locations of the nearby sensitive receivers, and monitoring procedures;
- Carry out random sample check and audit on monitoring data and sampling procedures, etc;
- Conduct random site inspection;
- Review the effectiveness of environmental mitigation measures and project environmental performance;
- On an as-need basis, verify and certify the environmental acceptability of the construction methodology (both temporary and permanent works), relevant design plans and submissions under the environmental permit. Where necessary, the IEC should agree in consultation with the ET and the Contractor least impact alternative;
- Check complaint cases and the effectiveness of corrective measures;
- Verify EM&A report certified by the ET Leader; and
- Feedback audit results to RE/ET according to the Event/Action Plan.

Environmental Team (ET)

2.06 The ET should conduct the EM&A programme and ensure the Contractor's compliance with the project's environmental performance requirements during construction. The ET should plan, organize and manage the implementation of the EM&A programme and ensure that the EM&A works are undertaken to the required standard.

2.07 The ET should be led and managed by the ET Leader. The ET Leader should have relevant

professional qualifications in environmental control and possess at least 7 years' experience in EM&A. The ET Leader should be responsible for the implementation of the EM&A programmes in accordance with the EM&A requirements. The duties and responsibilities of the ET include:

- Sampling, analysis and statistical evaluation of monitoring parameters;
- Environmental site surveillance;
- Inspection and audit of compliance with environmental protection, and pollution prevention and control regulations;
- Assess the effectiveness of the environmental mitigation measures implemented;
- Monitor compliance with the environmental protection clauses/specifications in the Contract;
- Review construction programme and comment as necessary;
- Review work methodologies which may affect the extent of environmental impact during the construction phase and comment as necessary;
- Complaint investigation, evaluation and identification of corrective measures;
- Liaison with the IEC on all environmental performance matters, and timely submission of all relevant EM&A proforma for IEC's approval; and
- Advice to Contractor on environmental improvement, awareness and enhancement matters etc.

The Contractor

- 2.08 The Contractor should report to the RE. The duties and responsibilities of the Contractor are:
- Comply with the relevant contract conditions and specifications on environmental protection
 - Participate in the site inspections undertaken by the ET;
 - Provide assistance to ET to carry out monitoring;
 - Provide requested information to the ET in the event of any exceedance in the environmental criteria (Action/Limit levels);
 - Submit proposals on mitigation measures in case of exceedances of Action and Limit levels in accordance with the Event / Action Plans; and
 - Cooperate with the ET in providing all the necessary information and assistance for completion of the complaint investigation works. If mitigation measures are required following the investigation, the Contractor should promptly carry out these measures.

SUMMARY OF ENVIRONMENTAL SUBMISSIONS

- 2.09 In according with the EP stipulation, the required documents submission status to EPD for retention as listed below:

Table 2-1 Submission/Set-up Status of the EP Requirements

| EP Condition | Submission | Status |
|--------------|--|-------------------|
| 2.3 | Management Organization of Main Construction Companies | Submitted |
| 2.7 | Landscape Plan | Submitted |
| 3.3 | Baseline Monitoring Report (TCS00704/14/600/R0010v4) | Submitted |
| 4.2 | Internet website | not yet effective |

- 2.10 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project are presented in **Table 2-2**.

Table 2-2 Status of Environmental Licenses and Permits of the Project

| Item | Description | License/Permit Status |
|------|--|--|
| 1 | Air pollution Control (Construction Dust) Regulation | NA |
| 2 | Chemical Waste Producer Registration - Waste Producers Number | WPN:5213-131-K3099-01 Approved on 14/05/2014 |
| 3 | Water Pollution Control Ordinance - Discharge License | License no.: WT00019539-2014 Approved on 16/07/2014 Valid to: 31/07/2019 |
| 4 | Waste Disposal Regulation - Billing Account for Disposal of Construction Waste | Account no.: 7019837 Approved on 30/04/2014 |

CONSTRUCTION PROGRESS

2.11 The Project was commenced on 28 August 2014. In this Reporting Period, construction activities conducted are listed below. Moreover, the master construction program is enclosed in *Appendix B*.

- Erect of hoarding of SBC and playground
- Sheet pile installation works
- Connection of temporary power supply
- Installation of water tank for temporary water supply
- Dismantled Two floodlights in SBC
- Demolished the concrete footings
- Installation of two temporary floodlights
- Install the compressible filler on the surface of hoarding
- Protection work for electric cables expose

3 ENVIRONMENTAL IMPACT MONITORING REQUIREMENT

3.01 The ET will implement the EM&A programme in accordance with the requirements in EMAP. Details of the EM&A programme are presented in the following sub-sections.

MONITORING PARAMETERS

3.02 The EM&A impact monitoring program covers the following environmental aspects:

- Air Quality; and
- Construction noise

3.03 A summary of the monitoring parameters is presented in *Table 3-1*:

Table 3-1 Summary of the monitoring parameters of EM&A Requirements

| Environmental Issue | Parameters |
|---------------------|---|
| Air Quality | <ul style="list-style-type: none"> • 24-hour Total Suspended Particulate (hereinafter '24-hour TSP') • 1-hour TSP monitoring (*) |
| Construction Noise | <ul style="list-style-type: none"> • A-weighted equivalent continuous sound pressure level (30min) (hereinafter 'L_{eq(30min)}' during the normal working hours) |

Remarks:

(*) In case 24-hour TSP exceed the air quality criteria to be carried out

MONITORING LOCATIONS

3.04 According to Sections 2.3 and 3.4 of the EMAP attached to the Project Profile (Register No. PP-472/2012), construction noise and air quality monitoring location is required to be set up at Hennessy Building and Chiu Hin Mansion. In early May 2014, site visit was conducted to select suitable locations to carry out relevant noise and air monitoring for the EM&A Programme. It was noted that both Hennessy Building and Chiu Hin Mansion are residential buildings and only the 1/F to 2/F of the buildings could be accessed which are commercial premises. It is not possible to set up the monitoring station at upper floors inside the residential apartment which will cause nuisance to the residents. Finally, two locations at lower floor were selected which access were successfully granted by the premises occupiers. The monitoring stations proposed for the Project are summarized *Table 3-2* and illustrated in *Appendix C*.

Table 3-2 Air and Noise Monitoring Locations

| Aspect | Monitoring Location | Location ID | Address | Description |
|--------------------|---------------------|-------------|------------------------------------|--------------------------------|
| Air Quality | Chiu Hin Mansion | A1 | balcony at 1/F of Chiu Hin Mansion | ASR close to the Project site |
| Construction Noise | Hennessey Building | N1 | 2/F floor of Hennessey Building | NSR facing to the Project site |
| | Chiu Hin Mansion | N2 | balcony at 1/F of Chiu Hin Mansion | NSR facing to the Project site |

MONITORING FREQUENCY AND PERIOD

3.05 The requirements of impact monitoring are stipulated in the EMAP and presented as follows.

Air Quality

3.06 Frequency of impact air quality monitoring is as follows:

- 24-hour TSP Once every 6 days during course of works.

3.07 In case of non-compliance with the air quality criteria, a more frequent monitoring exercise adopting 1-hour TSP monitoring undertaken when the highest dust impact occurs, as specified in the Event and Action Plan, should be conducted within 24 hours after the result is obtained. This additional monitoring should be continued until excessive dust emission or the deterioration in air quality is rectified.

Construction Noise

- 3.08 One set of $L_{eq(30min)}$ as 6 consecutive $L_{eq(5min)}$ between 0700-1900 hours on normal weekdays and once every week during course of works. If construction work necessary to carry out at other time periods, i.e. restricted time period (19:00 to 07:00 the next morning and whole day on public holidays) (hereinafter referred as “the restricted hours”), 3 consecutive $L_{eq(5min)}$ measurement will depended CNP requirements to undertake. Supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.

MONITORING EQUIPMENT

Air Quality Monitoring

- 3.09 The 24-hour TSP shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. A direct reading dust meter is used to measure 1-hour TSP air quality in case of non-compliance with air quality criteria of the 24-Hour TSP measurement.
- 3.10 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory. All equipment to be used for air quality monitoring is listed in **Table 3-3**.

Table 3-3 Air Quality Monitoring Equipment

| Equipment | Model |
|-------------------------|---|
| 24-hour TSP | |
| High Volume Air Sampler | TISCH High Volume Air Sampler, HVS Model TE-5170 |
| Calibration Kit | TISCH Model TE-5028A |
| 1- hour TSP | |
| Portable Dust Meter | TSI Model 8520 DustTrak Aerosol Monitor / Aerocet 531 Handheld Particle Mass Profiler & Counter / Sibata LD-3A Laser Dust Monitor |

- 3.11 According to the EMAP, wind data monitoring equipment shall also be provided and set up for logging wind speed and wind direction near the dust monitoring locations. The equipment installation location shall be proposed by the ET and agreed with the IEC. For installation and operation of wind data monitoring equipment, the following points shall be observed:
- 1) The wind sensors should be installed 10 m above ground so that they are clear of obstructions or turbulence caused by buildings.
 - 2) The wind data should be captured by a data logger. The data shall be downloaded for analysis at least once a month.
 - 3) The wind data monitoring equipment should be re-calibrated at least once every six months.
 - 4) Wind direction should be divided into 16 sectors of 22.5 degrees each.
- 3.12 Although ET was successful granted HVS installation premises, however, the owners rejected to provide premises for wind data monitoring equipment installation.
- 3.13 In this situation, the ET proposed alternative methods to obtain representative wind data. Meteorological information as extracted from “the Hong Kong Observatory King’s Park Station” is alternative method to obtain representative wind data. For King’s Park Station, it also can provide the humidity, rainfall, and air pressure and temperature etc. meteorological information. In Hong Kong of a lot development projects, weather information extracted from Hong Kong Observatory is common alternative method if weather station installation not allowed.
- 3.14 Although there are other closer weather stations, King’s Park Station was selected as it is the nearest weather station that measures all the relevant parameters mentioned above. Moreover, the ET has compared the data among the stations, and concluded that there is minimal difference between meteorological data collected at the King’s Park station and other stations.

Construction Noise Monitoring

- 3.15 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m s⁻¹. Furthermore, an acoustic calibrator and sound level meter shall be calibrated yearly.
- 3.16 Noise monitoring equipment to be used for monitoring is listed in **Table 3-4**.

Table 3-4 Construction Noise Monitoring Equipment

| Equipment | Model |
|-------------------------------|-----------------------------|
| Integrating Sound Level Meter | B&K Type 2238 or Rion NL-14 |
| Calibrator | Rion NC-73 / B&K Type 4231 |
| Portable Wind Speed Indicator | Testo Anemometer |

MONITORING METHODOLOGY

24-hour TSP

- 3.17 The equipment used for 24-hour TSP measurement listed in Table 3-3, is a Tisch Environmental, Inc. Model TE-5170 TSP high volume air sampling system, which complied with EPA Code of Federal Regulation, Appendix B to Part 50. The High Volume Air Sampler (HVS) consists of the following:
- a. An anodized aluminum shelter;
 - b. A 8”x10” stainless steel filter holder;
 - c. A blower motor assembly;
 - d. A continuous flow/pressure recorder;
 - e. A motor speed-voltage control/elapsed time indicator;
 - f. A 7-day mechanical timer, and
 - g. A power supply of 220v/50 hz
- 3.18 The HVS is calibrated in accordance with the manufacturer’s instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5028A). The 24-hour TSP Monitoring using the HVS is also processed in accordance with the manufacturer’s Operations Manual. A valid calibration certificate of the calibration kit with the certificate of HVS calibrated is attached in **Appendix D**.
- 3.19 24-hour TSP is collected by the ET on filters of HVS and quantified by a local HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd (ALS), upon receipt of the samples. The ET keeps all the sampled 24-hour TSP filters in normal air conditioned room conditions, i.e. 70% HR (Relative Humidity) and 25°C, for six months prior to disposal. HOKLAS-accreditation certificate of ALS Technichem (HK) Pty Ltd (ALS) is provided in **Appendix E**.

Noise

- 3.20 Sound level meter listed in **Table 3-4** comply with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications, as recommended in Technical Memorandum (TM) issued under the Noise Control Ordinance (NCO), which was used for baseline noise monitoring. A valid of calibration certificates including sound level meter and an acoustic were shown in **Appendix D**.
- 3.21 The noise measurement is performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq). Leq(30min) in six consecutive Leq(5 min) measurements were used as the monitoring parameter.
- 3.22 During monitoring, the sound level meter mounted at the monitoring locations and oriented such that the microphone pointed to the site with the microphone facing perpendicular to the line of sight. The windshield was fitted for the measurement. For the monitoring, N1 and N2 are conducted 1 m from the exterior of the building façade.

- 3.23 Prior construction noise measurement, the accuracy of the sound level meter checked using an acoustic calibrator generating a known sound pressure level at a known frequency. The calibration level from before and after the noise measurement agrees to within 1.0dB.

DERIVATION OF ACTION/LIMIT (A/L) LEVELS

- 3.24 The baseline results form the basis for determining the environmental acceptance criteria for the impact monitoring. According to EMAP, the air quality and construction noise criteria were set up, namely Action and Limit levels are listed in *Tables 3-5* and *3-6*.

Table 3-5 Action and Limit Levels for Air Quality Monitoring

| Monitoring Station | Action Level ($\mu\text{g}/\text{m}^3$) | | Limit Level ($\mu\text{g}/\text{m}^3$) | |
|--------------------|---|-------------|--|-------------|
| | 1-hour TSP | 24-hour TSP | 1-hour TSP | 24-hour TSP |
| A1 | 290 | 162 | 500 | 260 |

Table 3-6 Action and Limit Levels for Construction Noise

| Monitoring Station | 0700-1900 hours on normal weekdays | |
|--------------------|---|-------------|
| | Action Level | Limit Level |
| N1 and N2 | When one documented complaint is received | 75 dB(A) |

Note: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the NCA have to be followed.

- 3.25 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan which presented in *Appendix F*.

DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.26 The all monitoring data were handled by the ET's in-house data recording and management system.
- 3.27 The monitoring data recorded in the equipment were downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data were input into a computerized database properly maintained by the ET. The laboratory results were input directly into the computerized database and checked by personnel other than those who input the data.
- 3.28 For monitoring parameters that require laboratory analysis, the local laboratory shall follow the QA/QC requirements as set out under the HOKLAS scheme for the relevant laboratory tests.

4 MONITORING RESULTS

4.01 The impact air quality and construction noise monitoring schedule is presented in [Appendix G](#) and the monitoring results are summarized in the following sub-sections.

24-HOUR TSP AIR QUALITY MONITORING RESULTS

4.02 In the Reporting Period, 7 occasions of 24-hours TSP monitoring was carried out at the proposed location A1 and the monitoring results are summarized in [Table 4-1](#). The detailed 24-hour TSP monitoring data are presented in [Appendix H](#) and the relevant graphical plots are shown in [Appendix I](#).

Table 4-1 Summary of 24-hour TSP Monitoring Results – A1

| Date | 24-hour TSP ($\mu\text{g}/\text{m}^3$) | Action Level | Limit Level |
|-----------------|--|--------------|-------------|
| 28-Aug-14 | 26 | 162 | 260 |
| 03-Sep-14 | 78 | | |
| 08-Sep-14 | 24 | | |
| 13-Sep-14 | 23 | | |
| 19-Sep-14 | 127 | | |
| 25-Sep-14 | 112 | | |
| 30-Sep-14 | 102 | | |
| Average (Range) | 70 (23 - 127) | | |

4.03 As shown in [Table 4-1](#), 24-hour TSP monitoring results are fluctuated below Action/ Limit Levels.

NOISE MONITORING RESULTS

4.04 In the Reporting Period, **10** occasions noise measurement was conducted at N1 and N2. The sound level meter was set in 1m from the exterior of the building façade at N1 and N2. Therefore, no façade correction (+3 dB(A) is added according to acoustical principles and EPD guidelines. The noise measurement results at N1 and N2 are listed in [Tables 4-2](#) and [4-3](#). The relevant graphical plots are shown in [Appendix I](#).

Table 4-2 Noise Monitoring Results of N1 (2/F floor of Hennessey Building), dB(A)

| Date | Start Time | 1st Leq5 | 2nd Leq5 | 3rd Leq5 | 4th Leq5 | 5th Leq5 | 6th Leq5 | Leq30min |
|--|------------|-----------------|----------|----------|----------|----------|----------|-----------|
| 03-Sep-14 | 09:49 | 74.3 | 74.3 | 74.3 | 74.9 | 73.9 | 74.7 | 74 |
| 10-Sep-14 | 10:16 | 67.0 | 67.7 | 67.2 | 71.9 | 77.3 | 71.8 | 72 |
| 15-Sep-14 | 10:08 | 68.9 | 69.2 | 67.2 | 67.0 | 68.1 | 67.3 | 68 |
| 22-Sep-14 | 10:14 | 75.1 | 67.1 | 67.9 | 71.7 | 70.9 | 67.8 | 71 |
| 29-Sep-14 | 10:25 | 69.2 | 72.5 | 71.2 | 68.8 | 66.7 | 66.2 | 70 |
| Limit Level of Construction Noise | | 75 dB(A) | | | | | | |

Table 4-3 Noise Monitoring Results of N2 (balcony at 1/F of Chiu Hin Mansion), dB(A)

| Date | Start Time | 1st Leq5 | 2nd Leq5 | 3rd Leq5 | 4th Leq5 | 5th Leq5 | 6th Leq5 | Leq30min |
|--|------------|-----------------|----------|----------|----------|----------|----------|-----------|
| 03-Sep-14 | 10:38 | 71.5 | 69.8 | 70.5 | 69.4 | 74.3 | 71.2 | 71 |
| 10-Sep-14 | 09:30 | 74.1 | 74.8 | 75.5 | 75.4 | 75.8 | 75.9 | 75 |
| 15-Sep-14 | 09:25 | 75.2 | 77.2 | 77.0 | 75.4 | 74.3 | 74.8 | 76 |
| 22-Sep-14 | 09:33 | 75.3 | 77.0 | 75.7 | 76.0 | 74.9 | 74.6 | 76 |
| 29-Sep-14 | 09:44 | 74.0 | 75.6 | 78.1 | 72.3 | 75.3 | 79.0 | 76 |
| Limit Level of Construction Noise | | 75 dB(A) | | | | | | |

4.05 Referred to above tables, no noise measurement result is higher than 75dB(A) was recorded at N1, but three occasions of noise measurement result higher than 75dB(A) were recorded at N2. As reviewed the baseline noise monitoring data of N2, high background noise is already exist. In

order to find the actual construction noise, the exceeded noise measurement results were adjusted by the baseline monitoring data show in *Table 4-4*.

Table 4-4 Adjustment of Construction Noise Level for N2, dB(A)

| Date | Time Period | Leq30min Measurement Record at the Receiver | Average Background Noise at the Receiver | Actual Construction Noise of the Project |
|-----------|-------------|---|--|--|
| 15-Sep-14 | 09:25 | 76 | 70 (09:00 – 10:00) | 75 |
| 22-Sep-14 | 09:33 | 76 | 70 (09:00 – 10:00) | 75 |
| 29-Sep-14 | 09:44 | 76 | 70 (09:00 – 10:00) | 75 |

Equation of Adjustment: $C = 10\log(10^{A/10} - 10^{B/10})$

Where:

A is noise level measurement at the receiver position;

B is average background noise at the measurement time at the receiver position; and

C is actual construction noise.

- 4.06 After the adjustment, the construction noise of the Project were indicated not exceed 75dB. No Notifications of Exceedances (NOEs) therefore was issued to the RE, IEC and the Main Contractor.
- 4.07 Furthermore, there is no noise complaint (Action Level exceedance) received by the MTRC and Contractor or EPD in the Reporting Period.
- 4.08 The meteorological data during the impact monitoring days are shown in [Appendix J](#).

5 WASTE MANAGEMENT

GENERAL WASTE MANAGEMENT

5.01 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

RECORDS OF WASTE QUANTITIES

5.02 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

5.03 The quantities of waste for disposal in this Reporting Period are summarized in *Table 5-1* and *5-2* and the Monthly Summary Waste Flow Table is shown in *Appendix K*.

Table 5-1 Summary of Quantities of Inert C&D Materials

| Type of Waste | Quantity | Disposal Location |
|--|----------|------------------------------------|
| C&D Materials (Inert) (ton) | 39.67 | - |
| Reused in this Contract (Inert) (ton) | 0 | - |
| Reused in other Projects (Inert) (ton) | 0 | - |
| Disposal as Public Fill (Inert) (ton) | 39.67 | Chai Wan Public Fill Barging Point |

Table 5-2 Summary of Quantities of C&D Wastes

| Type of Waste | Quantity | Disposal Location |
|---|----------|-------------------|
| Recycled Metal (kg) | 0 | - |
| Recycled Paper / Cardboard Packing (kg) | 0 | - |
| Recycled Plastic (kg) | 0 | - |
| Chemical Wastes (kg) | 0 | - |
| General Refuses (ton) | 0.67 | SENT Landfill |

5.04 In the Reporting Period, effluent generated from the Project was discharged in accordance with the Wastewater Discharge License.

5.05 Moreover, it is reminded that C&D materials would be reused on-site as far as practicable.

6 SITE INSPECTION

6.01 According to the EMAP, the environmental site inspection shall be formulation by ET Leader. Weekly environmental site inspections should carry out to confirm the environmental performance.

FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH

6.02 During the Reporting Period, six (6) occasions of weekly site inspections to evaluate site environmental performance was carried out by the RE, ET and the Contractor dated 28 August, 4, 11, 18, 25 and 29 September 2014 and the IEC was joined the site inspection **11 September 2014**.

6.03 No non-compliance was noted. However, two (2) observations and two (2) reminders were recorded by the ET. The findings / deficiencies observed during the weekly site inspections are listed in **Table 6-1**.

Table 6-1 Site Observations

| Date | Findings / Deficiencies | Follow-Up Status |
|-------------------|---|---|
| 28 August 2014 | <ul style="list-style-type: none"> • Construction waste was observed close to the retained trees; the Contractor should remove the waste immediately and fence off the tree protection zone properly. • Minor scratches were observed from the retained trees TR-10 and TR-11 due to machinery movement. As reminded the Contractor protect the retained trees within the working site. • Proper noise enclosure to prevent noise impact should be provided for generator. | <ul style="list-style-type: none"> • Has been rectified before site inspection dated 11 September 2014 • Only reminder • Only reminder |
| 4 September 2014 | <ul style="list-style-type: none"> • No new findings or deficiencies is found. However, prior deficiencies are still yet rectified. | <ul style="list-style-type: none"> • NA |
| 11 September 2014 | <ul style="list-style-type: none"> • No adverse environmental issue was observed. However, reminded the Contractor make copy of the EP with all relevant documents available on-site • The Contractor was reminded that quiet PMEs, noise barriers, noise enclosures, etc., should be provided as per EP Conditions | <ul style="list-style-type: none"> • The EP with all relevant documents has posted on site before site inspection dated 18 September 2014 • Only reminder |
| 18 September 2014 | <ul style="list-style-type: none"> • No adverse environmental issue was observed. | <ul style="list-style-type: none"> • NA |
| 25 September 2014 | <ul style="list-style-type: none"> • No adverse environmental issue was observed. | <ul style="list-style-type: none"> • NA |
| 29 September 2014 | <ul style="list-style-type: none"> • No adverse environmental issue was observed. | <ul style="list-style-type: none"> • NA |

6.04 Overall, site housekeeping such as daily cleanliness and weekly tidiness should be maintain in accordance with the PS requirements.

6.05 No site inspection was undertaken by external parties i.e. EPD and AFCD in this Reporting Month.

7 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

7.01 For the Project, no environmental complaint, summons and prosecution was received in the Reporting Period. The statistical summary table of environmental complaint is presented in *Tables 7-1, 7-2 and 7-3.*

Table 7-1 Statistical Summary of Environmental Complaints

| Reporting Period | Environmental Complaint Statistics | | | | | |
|------------------------------------|------------------------------------|------------|------------------|-------|-------|--------|
| | Frequency | Cumulative | Complaint Nature | | | |
| | | | Air | Noise | Water | Others |
| 28 August 2014 – 30 September 2014 | 0 | 0 | NA | NA | NA | NA |

Table 7-2 Statistical Summary of Environmental Summons

| Reporting Period | Environmental Summons Statistics | | | | | |
|------------------------------------|----------------------------------|------------|------------------|-------|-------|--------|
| | Frequency | Cumulative | Complaint Nature | | | |
| | | | Air | Noise | Water | Others |
| 28 August 2014 – 30 September 2014 | 0 | 0 | NA | NA | NA | NA |

Table 7-3 Statistical Summary of Environmental Prosecution

| Reporting Period | Environmental Prosecution Statistics | | | | | |
|------------------------------------|--------------------------------------|------------|------------------|-------|-------|--------|
| | Frequency | Cumulative | Complaint Nature | | | |
| | | | Air | Noise | Water | Others |
| 28 August 2014 – 30 September 2014 | 0 | 0 | NA | NA | NA | NA |

8 IMPLEMENTATION STATUS OF MITIGATION MEASURES

GENERAL REQUIREMENTS

- 8.01 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the EMAP covered the issues of dust, noise, water and waste and they are summarized presented in [Appendix L](#).
- 8.02 The Works under the Project shall be implementing the required environmental mitigation measures according to the EMAP as subject to the site condition. Environmental mitigation measures generally to be implemented by the Contractor is listed in [Table 8-1](#).

Table 8-1 Environmental Mitigation Measures

| Issues | Environmental Mitigation Measures |
|-------------------------------|--|
| Air Quality | <ul style="list-style-type: none"> Regular watering to reduce dust emissions from all exposed site surface, particularly during dry weather; Frequent watering for particularly dusty construction areas and areas close to air sensitive receivers; Cover all excavated or stockpile of dusty material by impervious sheeting or sprayed with water to maintain the entire surface wet; Public areas around the site entrance/exit had been kept clean and free from dust; and Tarpaulin covering of any dusty materials on a vehicle leaving the site. |
| Noise | <ul style="list-style-type: none"> Good site practices to limit noise emissions at the sources; Use of quiet plant and working methods; Use of site hoarding or other mass materials as noise barrier to screen the working site; Use of shrouds/temporary noise barriers to screen noise from relatively static PMEs; and Limiting as use one construction plant within worksite, where practicable. |
| Water Quality | <ul style="list-style-type: none"> Wastewater were appropriately treated by treatment facilities; Drainage channels were provided to convey run-off into the treatment facilities; and Drainage systems were regularly and adequately maintained. |
| Waste and Chemical Management | <ul style="list-style-type: none"> Excavated material should be reused on site as far as possible to minimize off-site disposal. Scrap metals or abandoned equipment should be recycled if possible; Waste arising should be kept to a minimum and be handled, transported and disposed of in a suitable manner; The Contractor should adopt a trip ticket system for the disposal of C&D materials to any designed public filling facility and/or landfill; and Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes. |
| Landscape and Visual | <ul style="list-style-type: none"> Clear demarcation of works area to prevent damages to existing trees in close proximity; Protection of all trees planned to be retained onsite; Preserving all affected trees by transplanting where practical. Tree transplanting application and tree removal application shall be submitted for approval in accordance with ETWB TCW 3/2006; and Screening of construction works by hoardings/noise barriers around Works area in visually unobtrusive colours. |
| General | <ul style="list-style-type: none"> The site was generally kept tidy and clean. |

TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

- 8.03 Construction activities as undertaken in the coming month for the Project lists below:

- Installation of temporary water and power supply for site
- Trial Trench Excavation Works
- Continue the sheet pile installation works
- Pumping test
- Excavation works for NBC
- Installation of Internal Hoarding and Block Work for New Audit Room
- Installation and Diversion E&M Service
- ABWF Works in WAC Station
- Concrete Deck Below Tram Track

KEY ISSUES FOR THE COMING MONTH

- 8.04 Key issues to be considered in the coming month of the Project include:
- Implementation of dust suppression measures at all times;
 - Potential wastewater quality impact due to surface runoff;
 - Potential fugitive dust quality impact due from the dry/loose/exposure soil surface/dusty material;
 - Disposal of empty engine oil containers within site area;
 - Ensure dust suppression measures are implemented properly;
 - Silt removal facilities should be regularly maintained;
 - Management of chemical wastes;
 - Discharge of site effluent and stockpiling or disposal of materials at this area are prohibited;
 - Follow-up of improvement on general waste management issues; and
 - Implementation of construction noise preventative control measures
- 8.05 In addition, mosquito control measures should be continued to prevent mosquito breeding on site.

9 CONCLUSIONS AND RECOMMENDATIONS

CONCLUSION

- 9.01 The construction of the Project as well as the EM&A Programme in relevant section was therefore commenced on **28 August 2014** to comply with the EP and EMAP requirements. This monthly EM&A report presenting the monitoring results and inspection findings in The Reporting Period from **28 August** to **30 September 2014**.
- 9.02 In the Reporting Period, **7** occasions of 24-hours TSP monitoring was conducted at A1. The monitoring results are all below the Action/ Limit Level. No Notifications of Exceedances (NOEs) or the associated corrective actions were therefore issued.
- 9.03 In the Reporting Period, total **10** occasions of noise measurement was conducted at N1 and N2. No noise measurement result is higher than 75dB(A) was recorded at N1, but three occasions of noise measurement result higher than 75dB(A) were recorded at N2. As reviewed the baseline noise monitoring data of N2, high background noise is already exist. In order to find the actual construction noise, the exceeded noise measurement results were adjusted by the baseline monitoring data. After adjustment, the construction noise levels of the Project were indicated below 75dB(A). No Notifications of Exceedances (NOEs) or the associated corrective actions were therefore issued. Furthermore, no noise complaint (which is an Action Level exceedance) was received.
- 9.04 No environmental complaint, notification of summons or successful prosecution was received in the Reporting Period.
- 9.05 Six (6) occasions of weekly site inspections to evaluate site environmental performance was carried out by the RE, ET and the Contractor dated 28 August, 4, 11, 18, 25 and 29 September 2014. and the IEC was joined the site inspection **11 September 2014**. No non-compliance was noted and only two (2) observations and two (2) reminders were recorded by the ET. In addition, it was reminded that good housekeeping practice should be maintained. The environmental performance of the Project was considered as satisfactory.
- 9.06 In the Reporting Period, no site inspection was undertaken by external parties i.e. EPD and AFCD.


RECOMMENDATIONS

- 9.07 During rainy season, muddy water and other water quality pollutants via site surface water runoff get into to public areas should be avoided. Mitigation measures for water quality should be properly implemented.
- 9.08 Construction noise should be a key environmental impact during the works. The noise mitigation measures such as use of quiet plants or temporary noise barrier installation at the construction noise predominate area should be implemented as accordance with the EMAP requirement.
- 9.09 Moreover, special pay attention should be the potential construction dust impact since the Project site is located at urban areas. The Contractor should fully implement the construction dust mitigation measures properly.
- 9.10 As remind that the Contractor shall be properly performed and maintained a daily cleaning and weekly tidiness. In addition, mosquito control should be kept to prevent mosquito breeding on site.

Appendix A

Project Site Layout Plan

C:\ProgramData\Bentley\MicroStation\B1\SELECTseries\WorkSpace\System\p1c1g\WTR_PDF_BW_COL_300DP.dgn
 Diecad: H051494 PRINTED BY: 20/06/2012 16:56
 MODELNAME: ENVY202056\NEX1050_2.7A_000.dgn
 PLOT DRW: J:\28245\REPORT\ENVY202056\NEX1050_2.7A_000.dgn

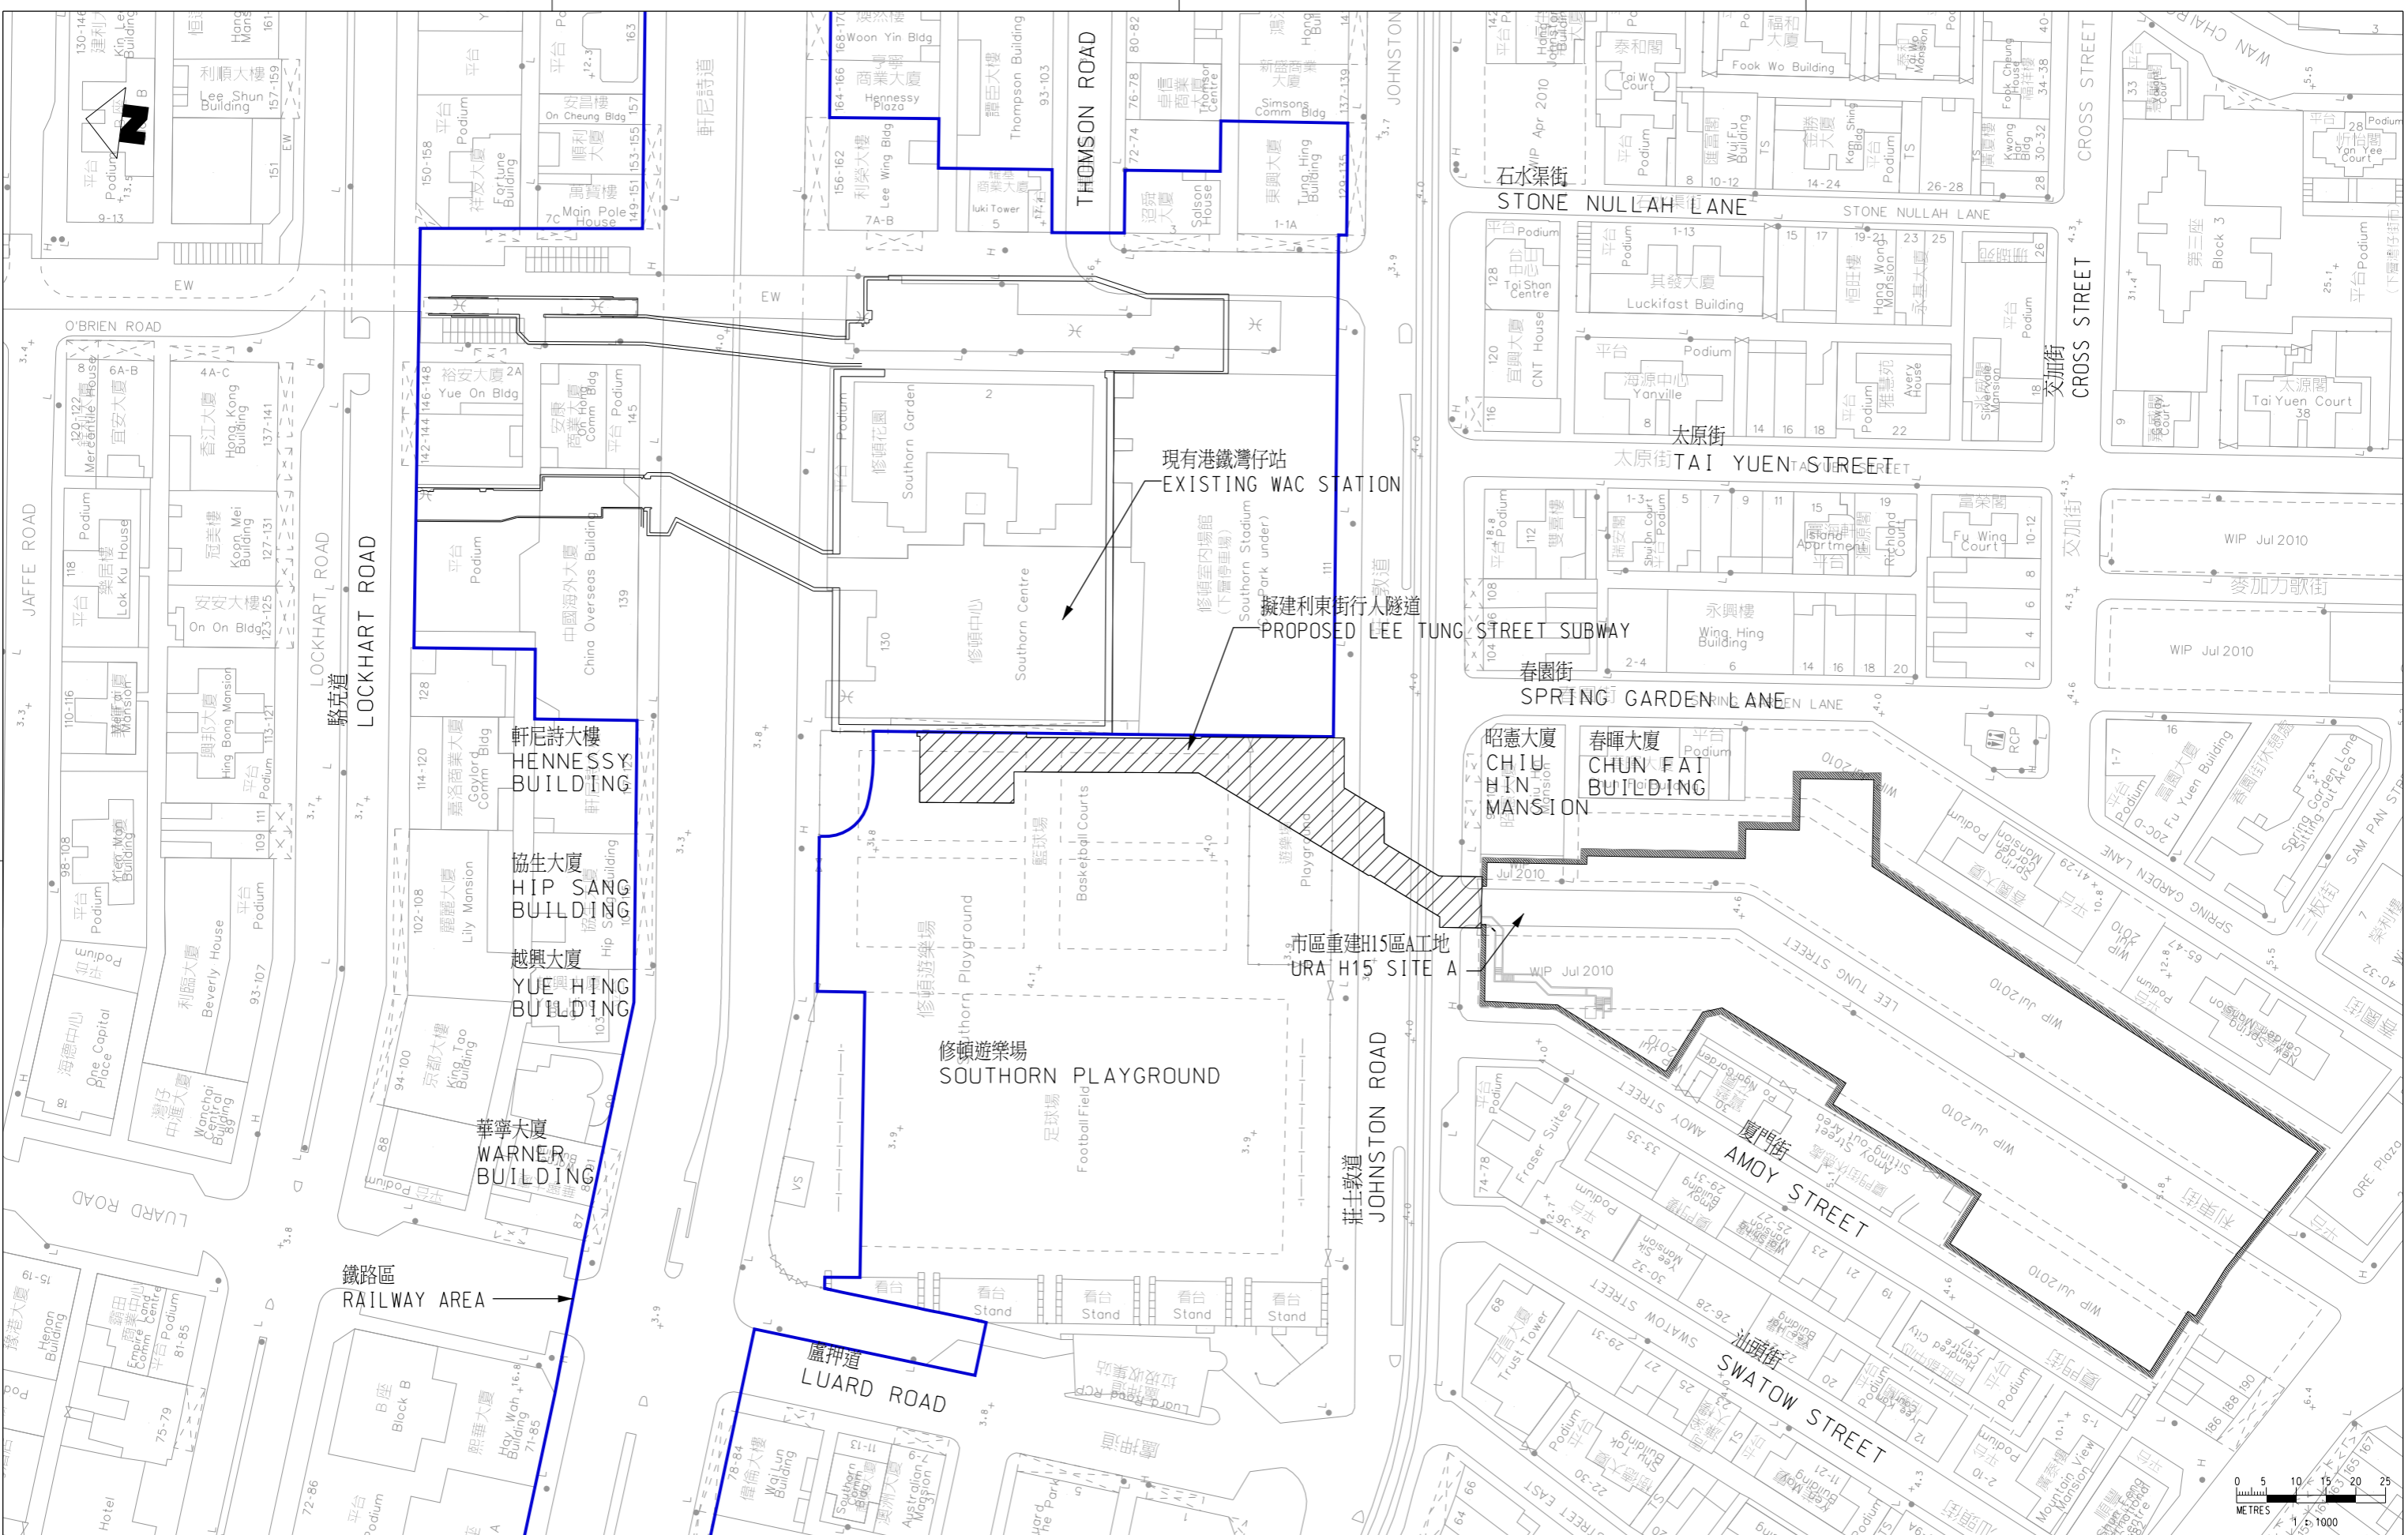

| REV | DESCRIPTION | BY | DATE | APPROVED | REV | DESCRIPTION | BY | DATE | APPROVED |
|-----|------------------|----|---------|----------|-----|-------------|----|------|----------|
| D | GENERAL REVISION | | 16MAY12 | AFK | | | | | |
| C | GENERAL REVISION | | 12AUG11 | AFK | | | | | |
| B | GENERAL REVISION | | 18JUL11 | AFK | | | | | |
| A | PROJECT PROFILE | | 04MAY11 | AFK | | | | | |

| | |
|----------|-----------|
| DRAWN | HO |
| DESIGNED | BW |
| CHECKED | BL |
| APPROVED | AFK |
| DATE | 04MAY2011 |

MTR

WAC STATION LEE TUNG STREET SUBWAY

ORIGINATOR

Mott MacDonald

20/F Two Landmark East
 100 How Ming Street
 Kowloon, Hong Kong
 Tel: +852 2808 8257
 Fax: +852 2807 1893
 www.mottmacdonald.com.hk

CADD REF. NEX1050_2.7A_0010.dgn

TITLE

CONSULTANCY AGREEMENT NO. NEX/1050
 DETAILED DESIGN FOR LEE TUNG STREET SUBWAY
 施工位置圖


SCALE 1:1000 (A3)

DRAWING NO. NEX1050/2.7A/001

REV. D

Appendix B

**Organization of the Project
and
Master Construction Programme**

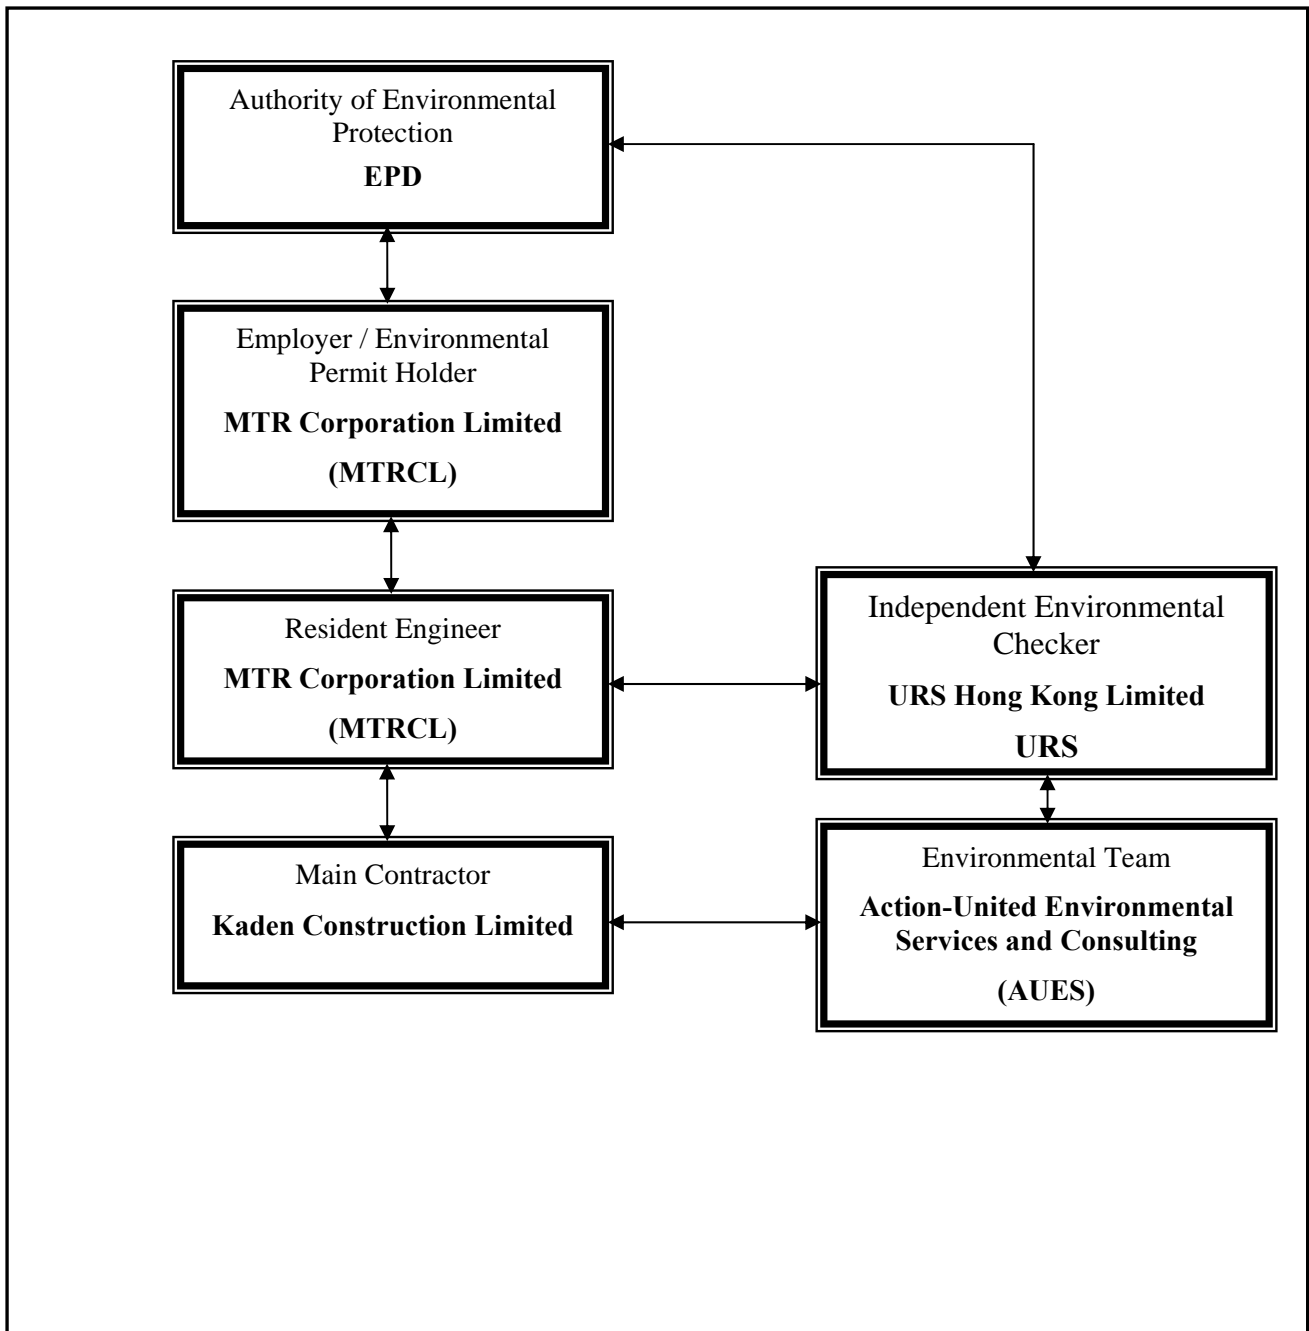

Contact Details of Key Personnel for the Project

| Organization | Project Role | Name of Key Staff | Tel No. | Fax No. |
|---------------------|-----------------------------------|----------------------------|----------------|----------------|
| MTRCL | Resident Engineer | Mr. Raymond Lee | 3547 0002 | 3547 0090 |
| URS | Independent Environmental Checker | Mr. Rodney Ip | 2410 3750 | 2428 9922 |
| KCL | Project Manager | Mr. Vincent, Kwan Chun Yin | 9833 1313 | 2770 4278 |
| KCL | Site Agent | Mr. Chan Kam Chuen | 6462 8910 | 2770 4278 |
| KCL | Environmental Officer | Ms. Ricci Poon Wai Tin | 9533 1115 | 2770 4278 |
| AUES | Environmental Team Leader | Mr. T. W. Tam | 2959 6059 | 2959 6079 |
| AUES | Environmental Consultant | Ms. Nicola Hon | 2959 6059 | 2959 6079 |
| AUES | Environmental Consultant | Mr. Ben Tam | 2959 6059 | 2959 6079 |

Legend:

MTRCL (Employer) – MTR Corporation Limited

MTRCL (Resident Engineer) – MTR Corporation Limited

KCL (Main Contractor) – Kaden Construction Limited


URS (IEC) – URS Hong Kong Limited

AUES (ET) – Action-United Environmental Services & Consulting

| C6593-13C WAC Station Lee Tung Street Subway Rev.B (30-Sep'14) | | Original | Planned Start | Planned Finish | Total Float | 2014 | | | | | | | | | | | | 2015 | | | | | | | | | | | | 2016 | | | | | | | | | | | | 2017 | | | | | | | | | | | |
|---|--|----------|-----------------|-----------------|-------------|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|--|--|--|
| Activity ID | Activity Name | Duration | | | | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | | | |
| C6593-13C WAC Station Lee Tung Street Subway Rev.B (30-Sep'14) | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Key Dates | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Commencement and Completion | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| KDCOMM | Commencement of the Works (14-Apr'14) | 0.00 | 14-Apr-14 08:00 | | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| KDCOMP | Completion of the Whole of the Works, No.Cal.Wk. 150 (26-Feb'17) | 0.00 | | 26-Feb-17 18:00 | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Specified Parts of the Works | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| KD2A | 2A - SBC Complete backfill, resurfacing, fencing, utilities, lighting and return to LCSD (28-Jun'15) | 0.00 | | 28-Jun-15 18:00 | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| KD2B | 2B - Complete all works at the 2 new Shop Kiosks and hand over to the Employer (1-May'16) | 0.00 | | 01-May-16 18:00 | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Programme Data / Interface Key Dates | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| INF.AFC | Interface Access for AFC, C&C DC in new AFC Audit Room inside WAC, Concourse Level (27-Apr'15) | 0.00 | 27-Apr-15 08:00 | | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| INF.H15 | Interface Access for Contract H15, All Levels, No.Cal.Wk. 120 (25-Jul'16) | 0.00 | 25-Jul-16 08:00 | | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| INF.SAMS | Interface Access for SAMS, Comms, MCS to All Areas, All Levels and Locations (10-Oct'16) | 0.00 | 10-Oct-16 08:00 | | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Site Area Possession and Return Dates | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Site Area Possession Date | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WAPW1 | Works Area 6593.W1, Within 3 months from commencement of works (14-Jul'14) | 0.00 | 14-Jul-14 08:00 | | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WAPW2 | Works Area 6593.W2, Within 9 months from commencement of works (14-Jan'15) | 0.00 | 14-Jan-15 08:00 | | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WAPW3 | Works Area 6593.W3, No later than 1 month after completion of reinstatement works at Works Area 6593.W1 | 0.00 | 08-Dec-16 08:00 | | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Site Area Return Date | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WARW1 | Works Area 6593.W1, Within 36 months from commencement of works (14-Apr'17) | 0.00 | | 07-Dec-16 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WARW2 | Works Area 6593.W2, Within 36 months from commencement of works (14-Apr'17) | 0.00 | | 07-Dec-16 18:00 | 81.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WARW3 | Works Area 6593.W3, Within 2 months after possession date of Works Area 6593.W3 | 0.00 | | 24-Feb-17 18:00 | 2.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Milestone Schedule | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Milestones A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA01 | A1 Approval of Preliminary Master Program, ICE, TTA, ELS & Temporary decking (3-Aug'14) | 0.00 | | 02-Aug-14 18:00 | 939.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA02 | A2 Approval of Design of Mined Tunnel ESS; Hoarding phase/plan; TW under TramTrack; QP, SAP, PMP, H&SP, EMP (2-Nov'14) | 0.00 | | 01-Nov-14 18:00 | 848.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA03 | A3 Satisfactory Implementation of Specified Plans (25-Jan'15) | 0.00 | | 24-Jan-15 18:00 | 764.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA04 | A4 Approval of excavation method under Tram Track; Satisfactory Implementation of PMS (3-May'15) | 0.00 | | 02-May-15 18:00 | 666.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA05 | A5 Approval of WAC D-wall demolition; Satisfactory Implementation of Specified Plans (2-Aug'15) | 0.00 | | 01-Aug-15 18:00 | 575.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA06 | A6 Satisfactory Implementation of PMS (1-Nov'15) | 0.00 | | 31-Oct-15 18:00 | 484.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA07 | A7 Satisfactory Implementation of Specified Plans (31-Jan'16) | 0.00 | | 30-Jan-16 18:00 | 393.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA08 | A8 AIP for T&C of BS and ABWF works; Satisfactory Implementation of PMS (1-May'16) | 0.00 | | 30-Apr-16 18:00 | 302.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA09 | A9 Satisfactory Implementation of Specified Plans (31-Jul'16) | 0.00 | | 30-Jul-16 18:00 | 211.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA10 | A10 AIP of Draft O&M manual and Draft As-built Drawings; Satisfactory Implementation of PMS (30-Oct'16) | 0.00 | | 29-Oct-16 18:00 | 120.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSA11 | A11 Approval of O&M manual and As-built drawings for the Works (26-Feb'17) | 0.00 | | 06-Jan-17 18:00 | 51.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Milestones B | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSB01 | B1 Excavate to +2.5 of Southern Basketball Court & Jonhston Road Westbound utilities support/diversions (2-Nov'14) | 0.00 | | 01-Nov-14 18:00 | 848.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSB02 | B2 SBC RC base slab, JR NFP & EB carriageway works (33%), underpinning of tram track completed (25-Jan'15) | 0.00 | | 31-Dec-14 18:00 | 788.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSB03 | B3 SBC RC roof slab, JR North footpath and EB carriageway works completed (3-May'15) | 0.00 | | 14-Apr-15 18:00 | 684.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSB04 | B4 SBC return to LCSD, North Basket ball court takeover, JR footpath&EB Carriageway formation level reached (2-Aug'15) | 0.00 | | 15-Jul-15 18:00 | 592.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSB05 | B5 NBC cofferdam, base slab under JR footpath and EB carriageway completed (1-Nov'15) | 0.00 | | 09-Oct-15 18:00 | 506.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSB06 | B6 NBC Formation excavation, TramTrack Mined tunnel; JR WB Car'way&SFP Formation & H15 Opening completed (31-Jan'16) | 0.00 | | 19-Jan-16 18:00 | 404.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSB07 | B7 NBC Roof slab; JR NFP & EB Carriageway; Under Tram Track; JR WB and SFP RC completed (1-May'16) | 0.00 | | 30-Apr-16 18:00 | 302.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSB08 | B8 ABWF degree 1; NBC- Resurfacing & reinstatement works completed (31-Jul'16) | 0.00 | | 03-May-16 18:00 | 299.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSB09 | B9 ABWF degree 3; Road reinstatement in JR & Hennessy Road completed (30-Oct'16) | 0.00 | | 17-Oct-16 18:00 | 132.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSB10 | B10 All works in Cost Centre B satisfactorily completed (26-Feb'17) | 0.00 | | 07-Dec-16 18:00 | 81.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Milestones C | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSC01 | C1 AIP BS detail design (2-Nov'14) | 0.00 | | 08-Sep-14 18:00 | 902.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSC02 | C2 AIP BS shop drawings (25-Jan'15) | 0.00 | | 20-Nov-14 18:00 | 829.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSC03 | C3 Order all BS equipment and materials (3-May'15) | 0.00 | | 09-Jan-15 18:00 | 779.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSC04 | C4 Complete all factory acceptance testings (29-Nov'15) | 0.00 | | 27-May-15 18:00 | 641.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSC05 | C5 Complete all delivery to site for ECS plant room (31-Jul'16) | 0.00 | | 22-Mar-16 18:00 | 341.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSC06 | C6 Complete all installation, T&C for New Subway (4-Dec'16) | 0.00 | | 07-Oct-16 18:00 | 142.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSC07 | C7 Complete and pass all statutory inspections, Operations Team (26-Feb'17) | 0.00 | | 07-Dec-16 18:00 | 81.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Milestones D | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSD01 | D1 New AFC Audit Room construction completed (3-May'15) | 0.00 | | 24-Nov-14 18:00 | 825.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSD02 | D2 Old AFC Audit Room and Maxim's/ Circle K kiosks demolished (31-Jan'16) | 0.00 | | 18-Nov-15 18:00 | 466.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSD03 | D3 Breakthrough into WAC (29-May'16) | 0.00 | | 15-Mar-16 18:00 | 348.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSD04 | D4 All works in Cost Centre D satisfactorily completed (31-Jul'16) | 0.00 | | 21-Apr-16 18:00 | 311.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Milestones E | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSE01 | E1- AFC gates and barrier relocation works completed (3-Jan'16) | 0.00 | | 22-Dec-15 18:00 | 432.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSE02 | E2- All structural A&A works for TIM completed (30-Oct'16) | 0.00 | | 29-Oct-16 18:00 | 120.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |



Preliminary Master Programme (Rev.B)



| Activity ID | Activity Name | Original Duration | Planned Start | Planned Finish | Total Float | 2014 | | | | | | | | | | | | 2015 | | | | | | | | | | | | 2016 | | | | | | | | | | | | 2017 | | | | | | | | | | | |
|---|---|-------------------|-----------------|-----------------|-------------|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|--|--|--|
| | | | | | | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | | | |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSE03 | E3- All works in milestone E completed (26-Feb'17) | 0.00 | | 29-Oct-16 18:00 | 120.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A. Preliminaries and General Items | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Design, ICE, Submission and Approval | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Design, ICE, BD Submission and Approval | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.ELS10 | A1 - ELS & Temporary Decking - Design, ICE, Submission to BD for Approval | 19.00 | 14-Apr-14 08:00 | 10-May-14 18:00 | 3.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.ELS11 | A1 - ELS & Temporary Decking - Review the submission | 28.00 | 12-May-14 08:00 | 13-Jun-14 18:00 | 3.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.ELS12 | A1 - ELS & Temporary Decking - Preparation of re-submission (If Require) | 14.00 | 14-Jun-14 08:00 | 30-Jun-14 18:00 | 3.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.ELS13 | A1 - ELS & Temporary Decking - BD Review, Resubmission if required, and Approval | 28.00 | 02-Jul-14 08:00 | 02-Aug-14 18:00 | 3.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.ELS20 | A1 - ELS - Verification (based on 4 additional SI. AD-01 to AD-04), ICE | 20.00 | 25-Jul-14 08:00 | 16-Aug-14 18:00 | 18.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.ELS21 | A1 - ELS - Verification (based on 4 additional SI. AD-01 to AD-04), ICE, Submission & Approval | 28.00 | 18-Aug-14 08:00 | 19-Sep-14 18:00 | 18.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A04.MIT10 | A4 - Excavation method under tram track and TW design - Prepare, ICE and submission to BD/ GEO for Approval | 39.00 | 14-Apr-14 08:00 | 04-Jun-14 18:00 | 28.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A04.MIT20 | A4 - Excavation method under tram track and TW design - Review submission | 60.00 | 05-Jun-14 08:00 | 14-Aug-14 18:00 | 28.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A04.MIT30 | A4 - Excavation method under tram track and TW design - Address comments, ICE & Resubmission (if required) | 24.00 | 15-Aug-14 08:00 | 12-Sep-14 18:00 | 28.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A04.MIT40 | A4 - Excavation method under tram track and TW design - Review & Approval (if required) | 30.00 | 13-Sep-14 08:00 | 20-Oct-14 18:00 | 28.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Design, ITC, TMLG Submission and Approval | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.TTM10 | TTMS - Submission to Members of TMLG for Approval, ref. ITT 6.2 | 4.00 | 14-Apr-14 08:00 | 17-Apr-14 18:00 | 13.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.TTM20 | TTMS - TMLG Meetings and Approval, Resubmission if required, RMO Applications | 55.00 | 22-Apr-14 08:00 | 27-Jun-14 18:00 | 13.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Contractor Submission and Approval | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Programming, Specified Plans and Hoarding Plan | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP080 | Submission schedule - Preparation & submission | 22.00 | 14-Apr-14 08:00 | 14-May-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP081 | Submission schedule - Review & Approval | 24.00 | 15-May-14 08:00 | 12-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP082 | Submission schedule - Preparation for Re-submission (If Require) | 12.00 | 13-Jun-14 08:00 | 26-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP083 | Submission schedule - Review and Approval (If Require) | 12.00 | 27-Jun-14 08:00 | 11-Jul-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP090 | Initial Three Month Rolling Program - Preparation & submission | 10.00 | 14-Apr-14 08:00 | 28-Apr-14 18:00 | 792.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP091 | Initial Three Month Rolling Program - Review & Approval | 24.00 | 29-Apr-14 08:00 | 28-May-14 18:00 | 792.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP092 | Initial Three Month Rolling Program - Preparation for Re-submission (If Require) | 12.00 | 29-May-14 08:00 | 12-Jun-14 18:00 | 792.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP093 | Initial Three Month Rolling Program - Review and Approval (If Require) | 12.00 | 13-Jun-14 08:00 | 26-Jun-14 18:00 | 792.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP10 | A1 Preliminary Master Program - Preparation & submission | 47.00 | 14-Apr-14 08:00 | 13-Jun-14 18:00 | 75.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP11 | A1 Preliminary Master Program - Review & Approval | 14.00 | 14-Jun-14 08:00 | 30-Jun-14 18:00 | 75.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP12 | A1 Preliminary Master Program - Preparation for Re-submission (If Require) | 14.00 | 02-Jul-14 08:00 | 17-Jul-14 18:00 | 75.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.PMP13 | A1 Preliminary Master Program - Review and Approval (If Require) | 14.00 | 18-Jul-14 08:00 | 02-Aug-14 18:00 | 75.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP10 | A1 Specified Plans (QP, SAP, PMS, H&SP, EP) - Submission and Approval | 27.00 | 14-Apr-14 08:00 | 20-May-14 18:00 | 107.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP20 | A1 Specified Plans - Review, Resubmission if required, and Approval | 30.00 | 21-May-14 08:00 | 25-Jun-14 18:00 | 107.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP210 | Environmental management plan - Preparation & submission | 22.00 | 14-Apr-14 08:00 | 14-May-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP211 | Environmental management plan - Review & Approval | 24.00 | 15-May-14 08:00 | 12-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP212 | Environmental management plan - Preparation for Re-submission (If Require) | 12.00 | 13-Jun-14 08:00 | 26-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP213 | Environmental management plan - Review and Approval (If Require) | 12.00 | 27-Jun-14 08:00 | 11-Jul-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP220 | Appoint Environmental team- submit for engineer approval | 22.00 | 14-Apr-14 08:00 | 14-May-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP221 | Appoint Environmental team - Review & Approval | 24.00 | 15-May-14 08:00 | 12-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP222 | Appoint Environmental team - Preparation for Re-submission (If Require) | 12.00 | 13-Jun-14 08:00 | 26-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP223 | Appoint Environmental team - Review and Approval (If Require) | 12.00 | 27-Jun-14 08:00 | 11-Jul-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP230 | Quality Plan - Preparation & submission | 22.00 | 14-Apr-14 08:00 | 14-May-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP231 | Quality Plan - Review & Approval | 24.00 | 15-May-14 08:00 | 12-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP232 | Quality Plan - Preparation for Re-submission (If Require) | 12.00 | 13-Jun-14 08:00 | 26-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP233 | Quality Plan - Review and Approval (If Require) | 12.00 | 27-Jun-14 08:00 | 11-Jul-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP240 | Health and Safety Plan - Preparation & submission | 22.00 | 14-Apr-14 08:00 | 14-May-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP241 | Health and Safety Plan - Review & Approval | 24.00 | 15-May-14 08:00 | 12-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP242 | Health and Safety Plan - Preparation for Re-submission (If Require) | 12.00 | 13-Jun-14 08:00 | 26-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP243 | Health and Safety Plan - Review and Approval (If Require) | 12.00 | 27-Jun-14 08:00 | 11-Jul-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP250 | System Assurance Plan - Preparation & submission | 22.00 | 14-Apr-14 08:00 | 14-May-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP251 | System Assurance Plan - Review & Approval | 24.00 | 15-May-14 08:00 | 12-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP252 | System Assurance Plan - Preparation for Re-submission (If Require) | 12.00 | 13-Jun-14 08:00 | 26-Jun-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.SPP253 | System Assurance Plan - Review and Approval (If Require) | 12.00 | 27-Jun-14 08:00 | 11-Jul-14 18:00 | 780.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A02.HRD100 | A2 Hoarding phase - Preparation & submission | 12.00 | 14-Apr-14 08:00 | 30-Apr-14 18:00 | 14.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A02.HRD101 | A2 Hoarding phase - Review & Approval | 24.00 | 02-May-14 08:00 | 30-May-14 18:00 | 14.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A02.HRD102 | A2 Hoarding phase - Preparation for Re-submission (If Require) | 12.00 | 31-May-14 08:00 | 14-Jun-14 18:00 | 14.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A02.HRD103 | A2 Hoarding phase - Review and Approval (If Require) | 12.00 | 16-Jun-14 08:00 | 28-Jun-14 18:00 | 14.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Implementation of Specified Plans | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A02.SPP11 | A2 Satisfactory Implementation of Quality Plan | 0.00 | | 01-Nov-14 18:00 | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A02.SPP12 | A2 Satisfactory Implementation of Quality Plan | 0.00 | | 01-Nov-14 18:00 | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A02.SPP13 | A2 Satisfactory Implementation of Quality Plan | 0.00 | | 01-Nov-14 18:00 | 0.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Preliminary Master Programme (Rev.B)



| Activity ID | Activity Name | Original Duration | Planned Start | Planned Finish | Total Float | 2014 | | | | | | | | | | | | 2015 | | | | | | | | | | | | 2016 | | | | | | | | | | | | 2017 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|---|--|-------------------|-----------------|-----------------|-------------|------|---|---|---|---|---|---|---|---|----|----|----|------|----|----|----|----|----|----|----|----|----|----|----|------|----|----|----|----|----|----|---|---|---|---|---|------|---|---|---|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|---|---|---|---|---|---|---|---|---|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|---|---|---|---|---|---|---|---|---|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|
| | | | | | | M | | | J | | | J | | | A | | | S | | | O | | | N | | | D | | | J | | | F | | | M | | | A | | | M | | | J | | | J | | | A | | | S | | | O | | | N | | | D | | | J | | | F | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | | | | | | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 | 17 | 18 | 19 | 20 | 21 | 22 | 23 | 24 | 25 | 26 | 27 | 28 | 29 | 30 | 31 | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 | 17 | 18 | 19 | 20 | 21 | 22 | 23 | 24 | 25 | 26 | 27 | 28 | 29 | 30 | 31 | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 | 17 | 18 | 19 | 20 | 21 | 22 | 23 | 24 | 25 | 26 | 27 | 28 | 29 | 30 | 31 | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 | 17 | 18 | 19 | 20 | 21 | 22 | 23 | 24 | 25 |
| TTM 6 - NBC, Playground, JnR North Footpath, Carriageway WB | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Preliminaries, Instrumentation, UU Diversions, etc. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.HRD06 | Stage 6 - Erect hoarding 52m, and water infill barriers | 6.00 | 08-Jul-15 08:00 | 14-Jul-15 18:00 | 3.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B06.0100 | Implement TTM6, trial trenches, instrumentation, UU diversions at North Footpath, etc. | 24.00 | 15-Apr-15 08:00 | 13-May-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Sheet Pile, Pipe Pile, Grouting, Decking | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B06.0200 | Sheet pile at JnR WB Carriageway, 23 x 21m, total 483m, 37t | 6.00 | 14-May-15 08:00 | 20-May-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B06.0240 | Pipe pile at Johnston Road WB Carriageway, 17 x 21m, total 357m | 38.00 | 21-May-15 08:00 | 07-Jul-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B06.0260 | Grouting of pipe pile at JnR WB Carriageway | 21.00 | 15-Jun-15 08:00 | 10-Jul-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B06.0265 | Jet grout soil blocks for mined tunneling at JnR WB Carriageway | 31.00 | 21-May-15 08:00 | 27-Jun-15 18:00 | 16.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B06.0270 | Temporary decking at JnR WB Carriageway | 15.00 | 11-Jul-15 08:00 | 28-Jul-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Mined Tunnel Underneath Tram Track | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Preliminaries, Horizontal Pipe Piles and Grouting | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW004 | 2 Months notification to HKT prior to construction of mined tunneling works | 72.00 | 06-Feb-15 08:00 | 09-May-15 18:00 | 28.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW006 | 3mT TAM Grout to 1.6m-extent from tunnel temporary extrados | 26.00 | 12-Jun-15 08:00 | 14-Jul-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW020 | Break through pipe piles & flame cut holes in sheet H pile | 6.00 | 08-Jul-15 08:00 | 14-Jul-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW030 | Drilling full periphery for grouting, approx. 12mL | 18.00 | 15-Jul-15 08:00 | 04-Aug-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW040 | 1.6mT TAM grouting surrounding extrados of proposed steel tube periphery, approx. 12mL | 18.00 | 18-Jul-15 08:00 | 07-Aug-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW050 | Install steel tube for full periphery | 18.00 | 22-Jul-15 08:00 | 11-Aug-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW060 | Pressure grouting to fill steel tube and drilled voids around steel periphery | 18.00 | 25-Jul-15 08:00 | 14-Aug-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW070 | Weld steel rib in front of pipe pile/ sheet pile wall & within steel periphery | 14.00 | 25-Jul-15 08:00 | 10-Aug-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW080 | Remove sheet H pile sections and strutting for tunnel heading excavation | 3.00 | 11-Aug-15 08:00 | 13-Aug-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW090 | Measure ground water flow and supplementary grouting | 2.00 | 14-Aug-15 08:00 | 15-Aug-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.TW100 | Install temporary face support works | 3.00 | 17-Aug-15 08:00 | 19-Aug-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| RC Structures | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.CS0010 | Blinding layer, smooth concrete and waterproofing, 2 bays | 3.00 | 20-Jan-16 08:00 | 22-Jan-16 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.CS0100 | RC Base Slabs - Smoothing concrete 250tk, waterproof membrane, cast slab, 68m^3 Concrete, ReBar 10.5T | 18.00 | 23-Jan-16 08:00 | 16-Feb-16 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.CS0200 | RC Walls - Smoothing concrete 250tkm waterproof membrane, cast wall, 26m^3 Concrete, ReBar 22.3T | 18.00 | 04-Feb-16 08:00 | 27-Feb-16 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.CS0300 | RC Top Slabs - Waterproof membrane, cast top slab, 23m^3 Concrete, ReBar 10.5T | 20.00 | 19-Feb-16 08:00 | 12-Mar-16 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.CS0900 | Completion of Mined Tunnel Structure & completion of whole tunnel structure | 0.00 | 14-Mar-16 08:00 | | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Mined Tunnel Excavation | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Top Bench | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.EX0110 | Excavate 1st 1/4 top bench 12x1m advance heading, shotcrete face, install steel frame/beam/column@1000c/c (135m3) | 24.00 | 20-Aug-15 08:00 | 16-Sep-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.EX0120 | Excavate 2nd 1/4 top bench 12x1m advance heading, shotcrete face, install steel frame/beam/column@1000c/c (135m3) | 24.00 | 03-Sep-15 08:00 | 02-Oct-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.EX0140 | Excavate 3rd 1/4 top bench 12x1m advance heading, shotcrete face, install steel frame/beam/column@1000c/c (135m3) | 36.00 | 03-Oct-15 08:00 | 14-Nov-15 18:00 | 13.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.EX0150 | Excavate last 1/4 top bench 12x1m advance heading, shotcrete face, install steel frame/beam/column@1000c/c (135m3) | 36.00 | 17-Oct-15 08:00 | 28-Nov-15 18:00 | 13.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Middle Bench | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.EX0155 | Excavate 1st 1/2 middle bench 12x1m advance heading, shotcrete face, install steel frame/beam/column@1000c/c (270m3) | 36.00 | 03-Oct-15 08:00 | 14-Nov-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.EX0160 | Excavate last 1/2 middle bench 12x1m advance heading, shotcrete face, install steel frame/beam/column@1000c/c (270m3) | 60.00 | 02-Nov-15 08:00 | 13-Jan-16 18:00 | 13.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Bottom Bench | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.EX0170 | Excavate 1st 1/2 bottom bench 12x1m advance heading, shotcrete face, install steel frame/beam/column@1000c/c (270m3) | 36.00 | 02-Nov-15 08:00 | 12-Dec-15 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.EX8874 | Excavate 1st last 1/2 bottom bench 12x1m advance heading, shotcrete face, install steel frame/beam/column@1000c/c(270m3) | 25.00 | 14-Dec-15 08:00 | 14-Jan-16 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Break Through Pipe Pile Wall | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.EX8878 | Break through 1st 1/2 pipe piles & flame cut sheet H pile | 18.00 | 27-Nov-15 08:00 | 17-Dec-15 18:00 | 9.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MIT.EX8882 | Break through remaining 1/2 pipe piles & flame cut sheet H pile | 17.00 | 30-Dec-15 08:00 | 19-Jan-16 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| TTM 7 - NBC, Playground, JnR North & South Footpath | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Preliminaries, Instrumentation, UU Diversions, etc. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.HRD07 | Stage 7 - Erect hoarding 18m, Remove hoarding 32m, and water infill barriers | 5.00 | 29-Jul-15 08:00 | 03-Aug-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B07.0100 | Implement TTM7 | 2.00 | 29-Jul-15 08:00 | 30-Jul-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Sheet Pile, Pipe Pile, Grouting, Decking | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B07.0200 | Sheet pile at JnR South Footpath, 10 x 21m, total 210m, 16t | 5.00 | 04-Aug-15 08:00 | 08-Aug-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B07.0270 | Temporary decking at JnR South Footpath | 10.00 | 10-Aug-15 08:00 | 20-Aug-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Pump Test, Excavation, ELS | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B07.0280 | Pumping test 5 | 12.00 | 21-Aug-15 08:00 | 03-Sep-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B07.0300 | Excavation & ELS, 700 m3 | 14.00 | 04-Sep-15 08:00 | 19-Sep-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B07.0310 | Hard core blanket 300tk, blinding layer 75tk, waterproof membrane | 12.00 | 10-Sep-15 08:00 | 23-Sep-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| RC Structures | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B07.0400 | RC Slab - Smoothing concrete 250tk, waterproof membrane, cast slab, 120m^3 Concrete, ReBar 6.0T | 28.00 | 17-Sep-15 08:00 | 22-Oct-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B07.0500 | RC Wall - Smoothing concrete 250tkm waterproof membrane, cast wall, 55m^3 Concrete, ReBar 19.3T | 34.00 | 03-Oct-15 08:00 | 12-Nov-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B07.0600 | RC Top Slab - Waterproof membrane, cast top slab, 55m^3 Concrete, ReBar 9.0T | 38.00 | 17-Oct-15 08:00 | 01-Dec-15 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Backfill and Miscellaneous Works | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B07.0700 | Backfill to ground level, cut sheet pile 2m depth below ground, reinstate road & footpath at EB & WB footpaths | 30.00 | 02-Dec-15 08:00 | 08-Jan-16 18:00 | 45.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| TTM 8 - NBC, Playground, JnR Carriageway EB Kerb Lane & WB | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

- Actual Level of Effort
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone

Preliminary Master Programme (Rev.B)



| Activity ID | Activity Name | Original Duration | Planned Start | Planned Finish | Total Float | 2014 | | | | | | | | | | | | 2015 | | | | | | | | | | | | 2016 | | | | | | | | | | | | 2017 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|--|---|-------------------|-----------------|-----------------|-------------|------|--|--|--|---|--|--|--|---|--|--|--|------|--|--|--|---|--|--|--|---|--|--|--|------|--|--|--|---|--|--|--|---|--|--|--|------|--|--|--|---|--|--|--|---|--|--|--|---|--|--|--|---|--|--|--|---|--|--|--|---|--|--|--|---|--|--|--|---|--|--|--|---|--|--|--|---|--|--|--|---|--|--|--|---|--|--|--|
| | | | | | | M | | | | J | | | | J | | | | A | | | | S | | | | O | | | | N | | | | D | | | | J | | | | F | | | | M | | | | A | | | | M | | | | J | | | | J | | | | A | | | | S | | | | O | | | | N | | | | D | | | | J | | | | F | | | |
| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| TTM 9 - NBC, Playground, JnR Carriageway EB Median Lane | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.HRD08 | Stage 8 - Erect hoarding 55m, Remove hoarding 24m, Relocate 1 no. gate, and water infill barriers | 8.00 | 09-Jan-16 08:00 | 18-Jan-16 18:00 | 45.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B08.0100 | Implement TTM8 | 6.00 | 09-Jan-16 08:00 | 15-Jan-16 18:00 | 45.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B08.0200 | Cut down sheetpiles at JnR Carriageway EB Kerb Lane & pipe piles at JnR Carriageway WB 2m below ground | 18.00 | 19-Jan-16 08:00 | 11-Feb-16 18:00 | 45.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B08.0700 | Backfill and reinstate | 18.00 | 12-Feb-16 08:00 | 03-Mar-16 18:00 | 45.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| TTM 10 - NBC, Playground | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.HRD09 | Stage 9 - Erect hoarding 14m, Remove hoarding 37m, Relocate 1 no. gate, and water infill barriers | 4.00 | 04-Mar-16 08:00 | 08-Mar-16 18:00 | 47.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B09.0100 | Implement TTM9 | 6.00 | 04-Mar-16 08:00 | 10-Mar-16 18:00 | 45.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B09.0200 | Cut down sheetpiles and pipe piles 2 m below ground at JnR Carriageway EB Median Lane and JnR Carriageway WB | 19.00 | 11-Mar-16 08:00 | 06-Apr-16 18:00 | 45.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B09.0700 | Backfill and reinstate | 22.00 | 07-Apr-16 08:00 | 03-May-16 18:00 | 45.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Subway ABWF Works | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| BAF.0010 | Subway ABWF works - Degree 1 (1st Batch) | 65.00 | 13-Jun-15 08:00 | 29-Aug-15 18:00 | 3.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| BAF.0011 | Subway ABWF works - Degree 1 (Remaining Batch) (31-Jul'14) | 80.00 | 31-Aug-15 08:00 | 04-Dec-15 18:00 | 3.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| BAF.0030 | Subway ABWF works - Degree 3 (1st Batch) | 70.00 | 30-Jan-16 08:00 | 28-Apr-16 18:00 | 107.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| BAF.0031 | Subway ABWF works - Degree 3 (2nd Batch) | 70.00 | 29-Apr-16 08:00 | 23-Jul-16 18:00 | 107.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| BAF.0032 | Subway ABWF works - Degree 3 (Remaining Batch)(30-Oct'16) | 70.00 | 25-Jul-16 08:00 | 17-Oct-16 18:00 | 107.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MB09p | B9 ABWF degree 3 - Programmed | 0.00 | | 17-Oct-16 18:00 | 107.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B3 Fresh Air Intake Facility | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Structure and ABWF | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B3.0010 | Fresh Air Intake Structure, 40D/20 14 m3, formwork 79 m2, reebar 2t | 36.00 | 27-Aug-15 08:00 | 09-Oct-15 18:00 | 14.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B3.0100 | Fresh Air Intake ABWF works, Waterproof membrane 45 m2, Tiling roof+wall&column 9+45m2, kerb 12m, louvre 3 nr. | 50.00 | 10-Oct-15 08:00 | 08-Dec-15 18:00 | 107.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B4 Smoke Extraction Facility | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Structure and ABWF | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B4.0010 | Smoke Extraction Structure, 40D/20 16 m3, formwork 127 m2, rebar 2t | 36.00 | 10-Oct-15 08:00 | 21-Nov-15 18:00 | 14.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B4.0100 | Smoke Extraction ABWF works, Waterproof membrane 70 m2, Tiling roof+wall&column 9+45m2, kerb 12m, louvre 1 nr. | 42.00 | 09-Dec-15 08:00 | 29-Jan-16 18:00 | 107.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B6 URA H15 Breakout | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Structure and ABWF | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B6.0010 | Preparation and Breaking out at URA H15, 7.5mW x 4.5mH | 36.00 | 03-Nov-15 08:00 | 14-Dec-15 18:00 | 117.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B6.0020 | URA H15 ABWF, Prepare surface 25m, plastering+screeding 25+8m2, tiling 17m2, kerb 2m, ceiling 8m3, cladding 9m2 | 60.00 | 15-Dec-15 08:00 | 29-Feb-16 18:00 | 117.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| INF.H15p | Interface Access for Contract H15, All Levels, No.Cal.Wk. 131 | 0.00 | | 29-Feb-16 18:00 | 117.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B7 Reprovisioning Works to Southern Playground | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| NBC and SBC at Works Area 6593.W3 (Stage 11 & Stage 12) | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.HRD11 | Stage 11 - Erect hoarding 66m, Erect 1 no. gate (Reinstatement NBC) | 4.00 | 08-Dec-16 08:00 | 12-Dec-16 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A01.HRD12 | Stage 12 - Erect hoarding, 58m, Remove hoarding 58m (Reinstatement SBC) | 6.00 | 18-Jan-17 08:00 | 24-Jan-17 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B7.NBC310 | W3 NBC - Excavaton 116 m3, remove existing basketball court surface 375 m2 | 4.00 | 13-Dec-16 08:00 | 16-Dec-16 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B7.NBC320 | W3 NBC - Reinstatement - Subgrade, rc slab/light fnd., EPDM surface coat 375m2, furnitures, etc. | 24.00 | 17-Dec-16 08:00 | 17-Jan-17 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B7.SBC310 | W3 SBC - Excavaton 116 m3, remove existing basketball court surface 375 m2 | 6.00 | 25-Jan-17 08:00 | 03-Feb-17 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B7.SBC320 | W3 SBC -Reinstatement - Subgrade, rc slab/light fnd., EPDM surface coat 375m2, furnitures, etc. | 18.00 | 04-Feb-17 08:00 | 24-Feb-17 18:00 | 1.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Play Area | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B7.PLA020 | Play Area - Reinstatement - Install equipments, safety mat 330 m2, etc. | 88.00 | 10-Nov-15 08:00 | 26-Feb-16 18:00 | 206.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Landscaping Works | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B7.LDS200 | Play Area - RC wall & footing, finish to match existing 160m, planter wall 197m, etc. | 40.00 | 21-Sep-15 08:00 | 09-Nov-15 18:00 | 25.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B7.LDS300 | Play Area - Landscaping, Shrubs 1198 nr, tree 17 nr. | 90.00 | 10-Nov-15 08:00 | 29-Feb-16 18:00 | 204.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B7.LDS900 | Playground - Joint inspection and handover to LCSD | 28.00 | 12-Sep-16 08:00 | 17-Oct-16 18:00 | 45.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B8 Ground Investigation Works | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B00.0110 | Confirmation of location of SI, PH01, by the Engineer | 1.00 | 14-Jul-14 08:00 | 14-Jul-14 18:00 | 35.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B00.0111 | Mobilization of SI rigs | 4.00 | 15-Jul-14 08:00 | 18-Jul-14 18:00 | 35.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B00.0120 | Site Investigation, PH01 | 8.00 | 19-Jul-14 08:00 | 28-Jul-14 18:00 | 35.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| B00.0130 | Site Investigation, Lab tests and report, and submission | 28.00 | 29-Jul-14 08:00 | 29-Aug-14 18:00 | 35.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C. Subway Building Services Works | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Design, Shop Drawings, Materials & Equipments Submission and Approval | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C1.0010 | BS Works - Design, Materials and Equipments - Submission & AIP (1st Batch) | 60.00 | 14-Apr-14 08:00 | 28-Jun-14 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C1.0015 | BS Works - Design, Materials and Equipments - Submission & AIP (Remaining) | 60.00 | 30-Jun-14 08:00 | 08-Sep-14 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C2.0010 | BS Works - Shop drawings - Submission & AIP (1st Batch) | 60.00 | 30-Jun-14 08:00 | 08-Sep-14 18:00 | 53.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C2.0015 | BS Works - Shop drawings - Submission & AIP (Remaining) | 60.00 | 10-Sep-14 08:00 | 20-Nov-14 18:00 | 53.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Procurement and Delivery of Materials and Equipments | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C3.0010 | BS Works - Procurement of all major building service equipments and materials (1st Batch) | 50.00 | 10-Sep-14 08:00 | 08-Nov-14 18:00 | 6.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |



Preliminary Master Programme (Rev.B)



| Activity ID | Activity Name | Original Duration | Planned Start | Planned Finish | Total Float | 2014 | | | | | | | | | | | | 2015 | | | | | | | | | | | | 2016 | | | | | | | | | | | | 2017 | | | | | | | | | | | |
|--|--|-------------------|-----------------|-----------------|-------------|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|------|---|---|---|---|---|---|---|---|---|---|---|------|--|--|--|--|--|--|--|--|--|--|--|
| | | | | | | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | A | M | J | J | A | S | O | N | D | J | F | M | | | | | | | | | | | | |
| Breaking Out WAC Station | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| D2070 | Breaking out WAC Station - Form opening, core holes 72 nr, chain cut 1225 x 900mm block 55 nr. | 90.00 | 25-Nov-15 08:00 | 15-Mar-16 18:00 | 8.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| WAC Station Modification Works | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| D1001 | Liaison with MTR and relevance parties for works in WAC station | 90.00 | 14-Apr-14 08:00 | 04-Aug-14 18:00 | 121.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| D1002 | Preparation works for works in WAC station | 12.00 | 05-Aug-14 08:00 | 18-Aug-14 18:00 | 121.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| D1010 | Internal Hoarding in WAC station (NTH) | 12.00 | 19-Aug-14 08:00 | 01-Sep-14 18:00 | 121.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| D1020 | Construct new AFC/Audit Room next to Entrance B1, B2, ABWF & BS Works (NTH) | 69.00 | 02-Sep-14 08:00 | 24-Nov-14 18:00 | 121.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| D1030 | Modification Works to existing AFC/Audit, Store & Kiosk 3 & 5 (NTH) | 84.00 | 05-May-15 08:00 | 13-Aug-15 18:00 | 13.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| D1040 | Modification to existing Kiosk 2 (NTH) | 80.00 | 14-Aug-15 08:00 | 18-Nov-15 18:00 | 13.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| D1050 | Relocate 4 Advertising Panels (NTH) | 10.00 | 19-Nov-15 08:00 | 30-Nov-15 18:00 | 93.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| D1060 | Install New Telephone Booth and associated works (NTH) | 36.00 | 14-Aug-15 08:00 | 24-Sep-15 18:00 | 57.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| INF.AFCp | Interface Access for AFC, C&C DC in new AFC Audit Room inside WAC, Concourse Level, No.Cal.Wk. 55 - Programmed | 0.00 | | 24-Nov-14 18:00 | 153.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Testing and Commissioning | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| D4090 | Testing and Commissioning | 28.00 | 16-Mar-16 08:00 | 21-Apr-16 18:00 | 8.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| KD2Bp | Specified Part 2B - Complete all works at the 2 new Shop Kiosks and hand over to the Employer - Programmed | 0.00 | | 21-Apr-16 18:00 | 8.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| E. WAC Station Improvement Works (Part C Works) | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Improvement Works to WAC Station | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| E1020 | Modify, provide & install new glass barrier to suit new AFC gates (NTH) | 40.00 | 17-Sep-15 08:00 | 05-Nov-15 18:00 | 94.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| E1030 | Provide and install additional AFC gates (NTH) | 40.00 | 06-Nov-15 08:00 | 22-Dec-15 18:00 | 94.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| E1040 | Provide builder works for TIMS relocation (NTH) | 80.00 | 16-Mar-16 08:00 | 24-Jun-16 18:00 | 28.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| E1050 | T&C by Designated Contractor for TIMS (NTH) | 30.00 | 25-Jun-16 08:00 | 30-Jul-16 18:00 | 28.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| E1060 | Make Good builder works for TIMS (NTH) | 75.00 | 01-Aug-16 08:00 | 29-Oct-16 18:00 | 28.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| MSE03p | E3- All works in milestone E completed - Programmed | 0.00 | | 29-Oct-16 18:00 | 28.00 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone


Preliminary Master Programme (Rev.B)



Appendix C

Monitoring Locations

C:\ProgramData\Bentley\MicroStation\18\SELECTseries\WorkSpace\System\p1c1g\MTR_PDF_BW_COL_3000P.dgn
 PLOT DRW: C:\ProgramData\Bentley\MicroStation\18\SELECTseries\WorkSpace\System\p1c1g\MTR_PDF_BW_COL_3000P.dgn
 MODELNAME: J:\2006\2006\REPORT\ENV\VPZ\2006\NE\1050_2_11_0050.dgn
 FILENAME: J:\2006\2006\REPORT\ENV\VPZ\2006\NE\1050_2_11_0050.dgn

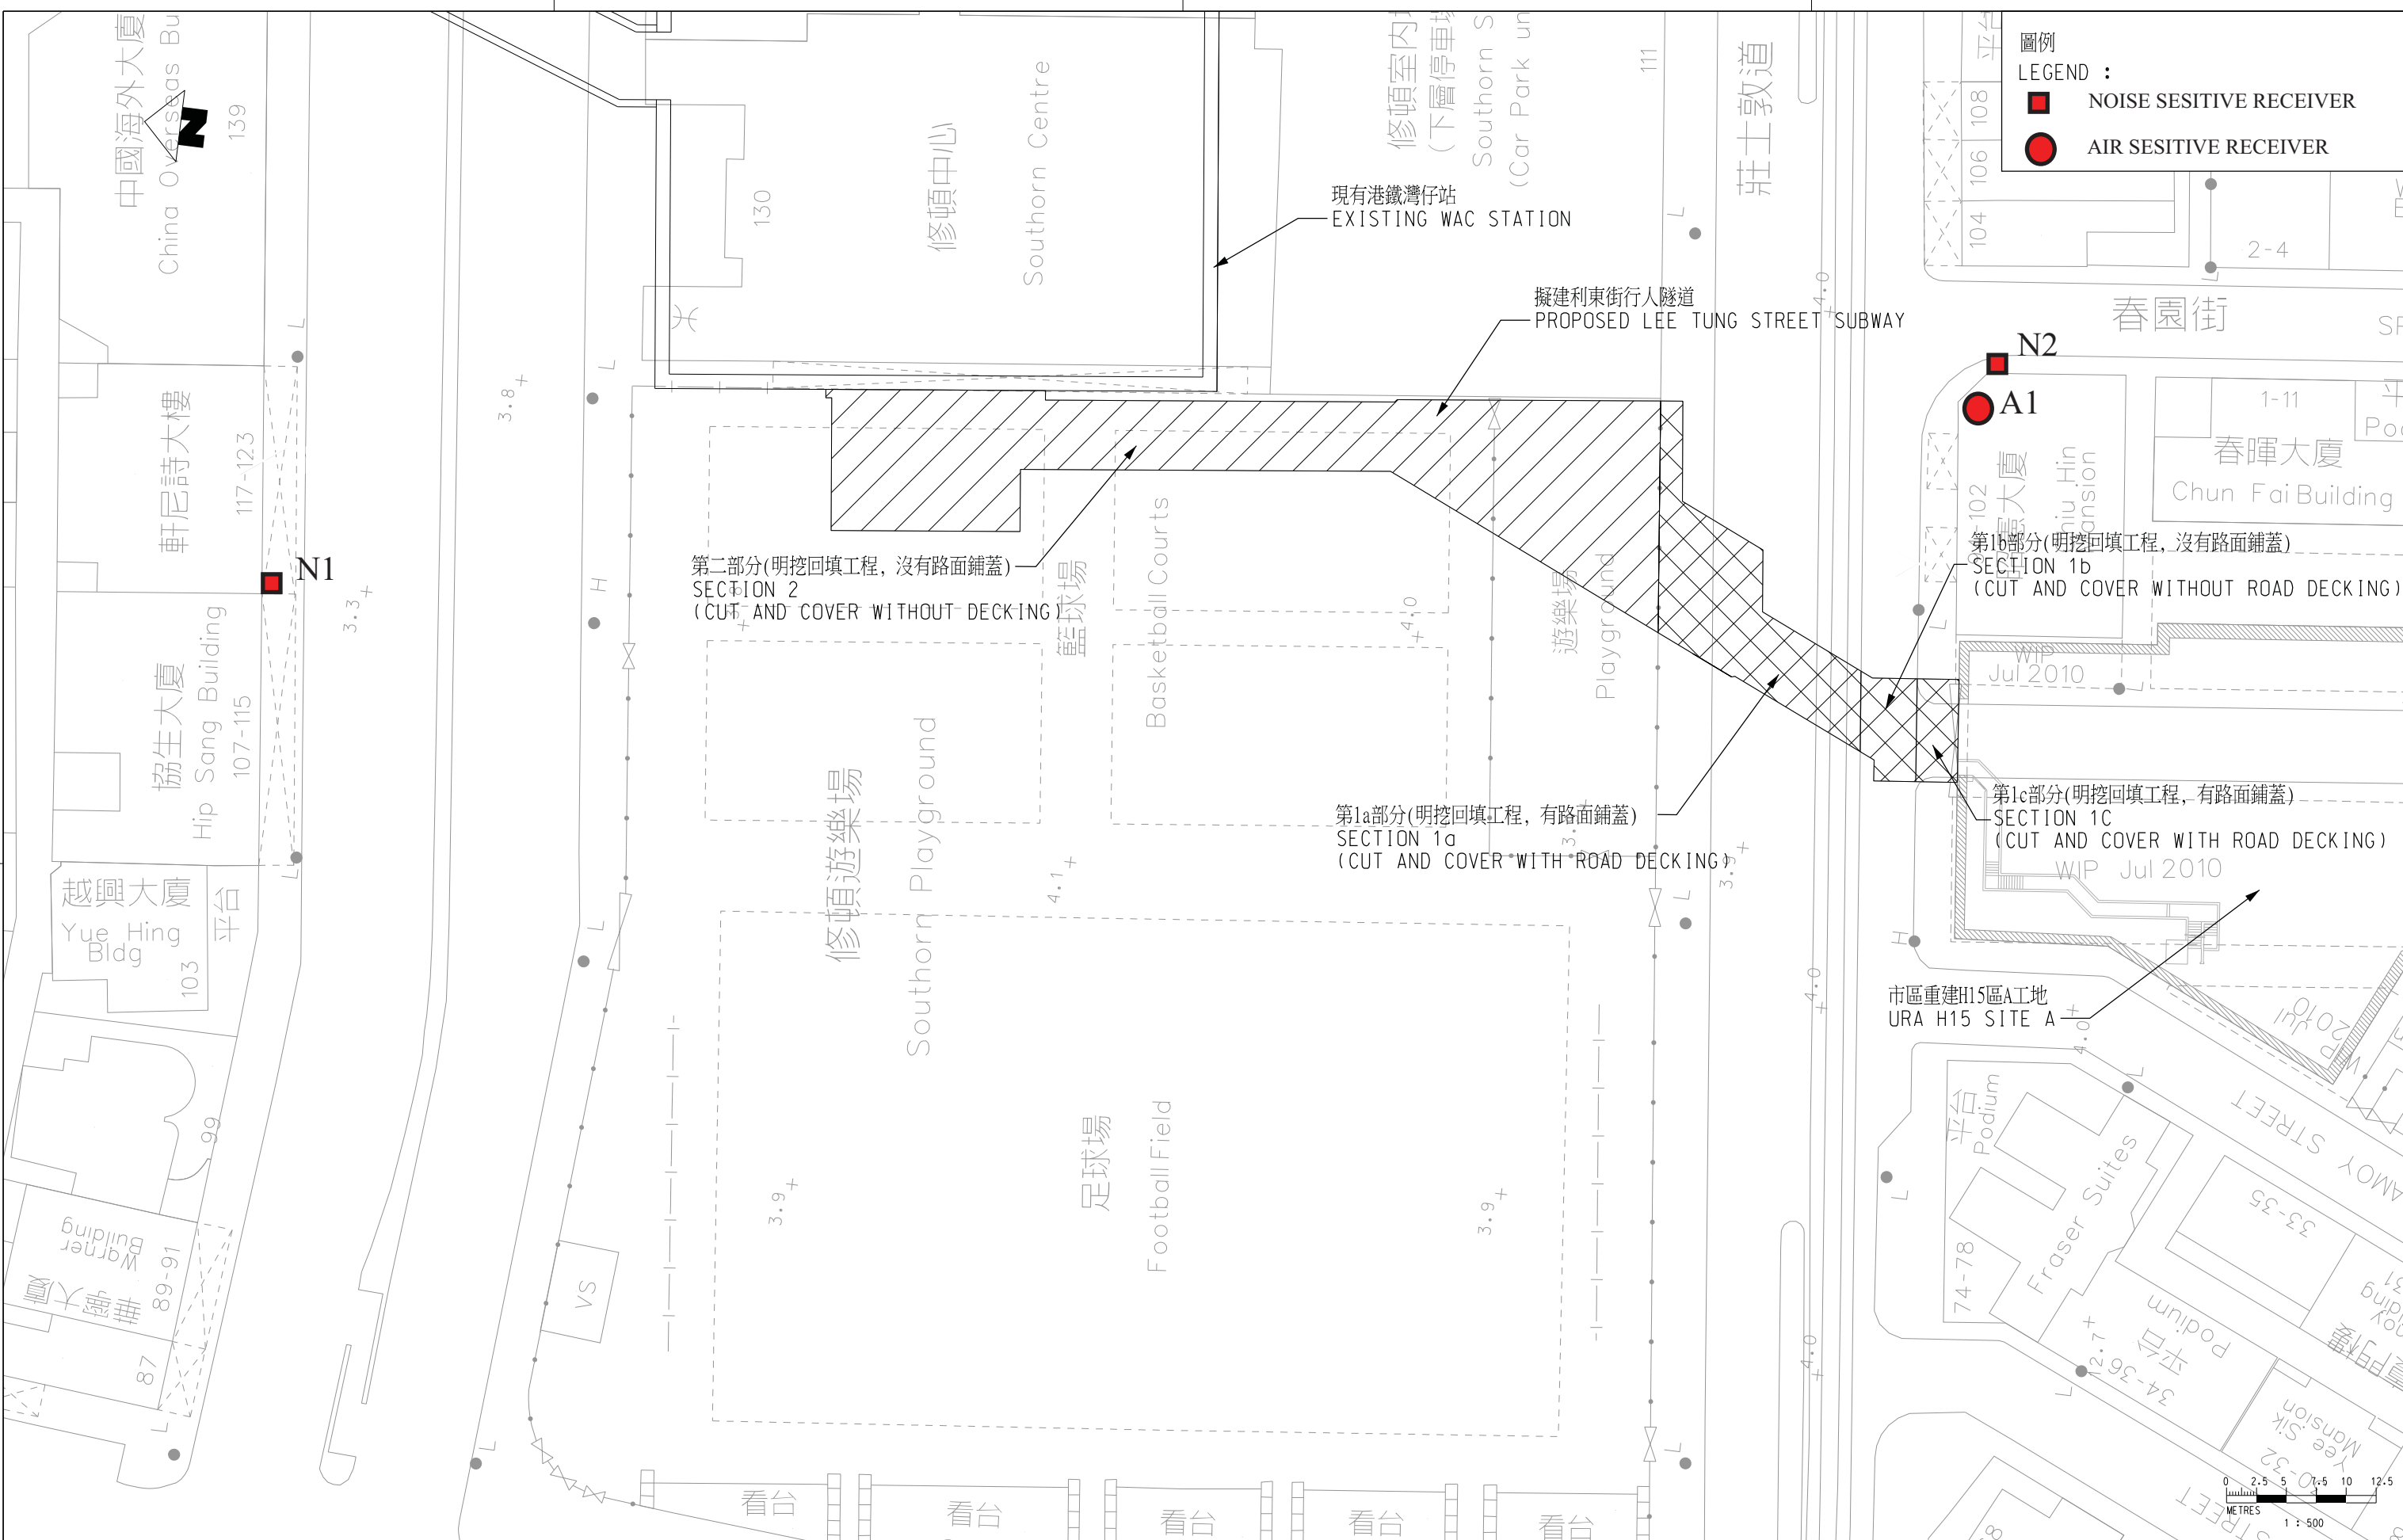

圖例
 LEGEND :

- NOISE SENSITIVE RECEIVER
- AIR SENSITIVE RECEIVER



| REV | DESCRIPTION | BY | DATE | APPROVED |
|-----|------------------|----|------|----------|
| D | GENERAL REVISION | | | |
| C | GENERAL REVISION | | | |
| B | GENERAL REVISION | | | |
| A | PROJECT PROFILE | | | |

| REV | DESCRIPTION | BY | DATE | APPROVED |
|-----|-------------|----|------|----------|
| | | | | |
| | | | | |
| | | | | |
| | | | | |

| | |
|----------|--|
| DRAWN | |
| DESIGNED | |
| CHECKED | |
| APPROVED | |
| DATE | |

MTR

WAC STATION LEE TUNG STREET SUBWAY

ORIGINATOR

Mott MacDonald

20F Two Landmark East
 100 Hoi Ming Street
 Kowloon, Hong Kong
 T +852 2808 5157
 F +852 2827 1823
 www.mottmac.com.hk

TITLE

CONSULTANCY AGREEMENT NO. NEX/1050
 DETAILED DESIGN FOR LEE TUNG STREET SUBWAY
 LOCATION OF NOISE AND AIR SENSITIVE RECEIVER

SCALE 1:500 (A3)

DRAWING NO.

REV.

Appendix D

**Calibration Certificate of
Monitoring Equipment**

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Chiu Hin Mansion

Date of Calibration: 4-Aug-14

Location ID : A1

Next Calibration Date: 4-Oct-14

Technician: Mr. Ben Tam

CONDITIONS

Sea Level Pressure (hPa)
Temperature (°C)

| |
|--------|
| 1004.2 |
| 29.5 |

Corrected Pressure (mm Hg)
Temperature (K)

| |
|--------|
| 753.15 |
| 303 |

CALIBRATION ORIFICE

Make-> TISCH
Model-> 5025A
Serial # -> 1612

Qstd Slope -> 2.00757
Qstd Intercept -> -0.01628

CALIBRATION

| Plate No. | H2O (L) (in) | H2O (R) (in) | H2O (in) | Qstd (m3/min) | I (chart) | IC corrected | LINEAR REGRESSION |
|-----------|--------------|--------------|----------|---------------|-----------|--------------|---|
| 18 | 6.0 | 6.0 | 12 | 1.713 | 53 | 51.98 | Slope = 31.3519 Intercept = -1.7775 Corr. coeff. = 0.9968 |
| 13 | 4.7 | 4.7 | 9.4 | 1.517 | 46 | 45.11 | |
| 10 | 3.6 | 3.6 | 7.2 | 1.329 | 42 | 41.19 | |
| 7 | 2.4 | 2.4 | 4.8 | 1.086 | 32 | 31.38 | |
| 5 | 1.4 | 1.4 | 2.8 | 0.832 | 25 | 24.52 | |

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta)) - b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)] - b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

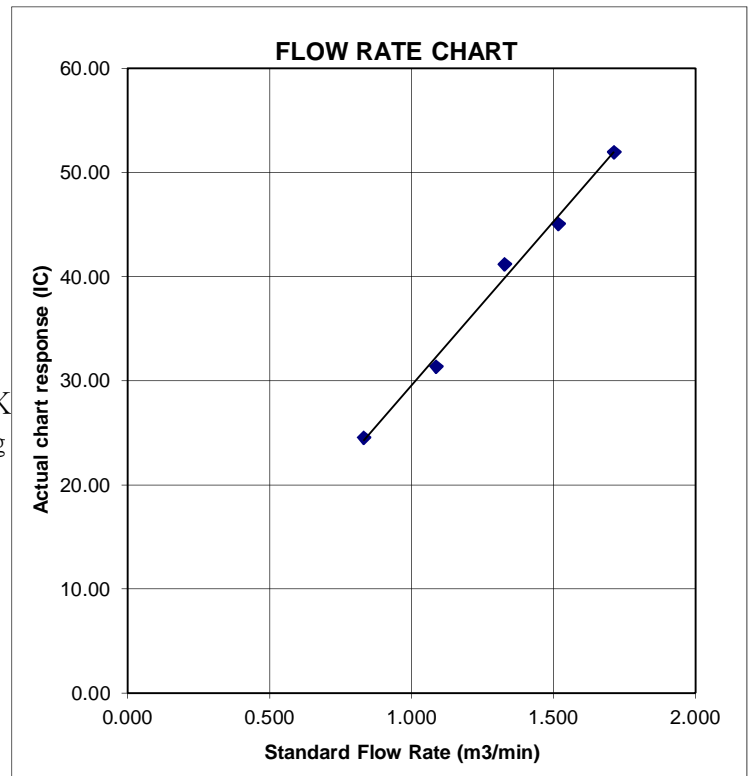



TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE
 VILLAGE OF CLEVELAND, OH
 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Apr 07, 2014 Rootmeter S/N 0438320 Ta (K) - 294
 Operator Tisch Orifice I.D. - 1612 Pa (mm) - 742.95

| PLATE OR Run # | VOLUME START (m3) | VOLUME STOP (m3) | DIFF VOLUME (m3) | DIFF TIME (min) | METER DIFF Hg (mm) | ORFICE DIFF H2O (in.) |
|----------------|-------------------|------------------|------------------|-----------------|--------------------|-----------------------|
| 1 | NA | NA | 1.00 | 1.3940 | 3.2 | 2.00 |
| 2 | NA | NA | 1.00 | 0.9790 | 6.4 | 4.00 |
| 3 | NA | NA | 1.00 | 0.8800 | 7.8 | 5.00 |
| 4 | NA | NA | 1.00 | 0.8350 | 8.8 | 5.50 |
| 5 | NA | NA | 1.00 | 0.6910 | 12.7 | 8.00 |

DATA TABULATION

| Vstd | (x axis) Qstd | (y axis) | Va | (x axis) Qa | (y axis) |
|--|---------------|----------|---|-------------|----------|
| 0.9866 | 0.7077 | 1.4077 | 0.9957 | 0.7142 | 0.8896 |
| 0.9823 | 1.0034 | 1.9908 | 0.9914 | 1.0127 | 1.2581 |
| 0.9804 | 1.1140 | 2.2258 | 0.9894 | 1.1243 | 1.4066 |
| 0.9791 | 1.1726 | 2.3345 | 0.9881 | 1.1834 | 1.4753 |
| 0.9739 | 1.4094 | 2.8155 | 0.9829 | 1.4224 | 1.7793 |
| Qstd slope (m) = 2.00757 | | | Qa slope (m) = 1.25710 | | |
| intercept (b) = -0.01628 | | | intercept (b) = -0.01029 | | |
| coefficient (r) = 0.99989 | | | coefficient (r) = 0.99989 | | |
| y axis = $\text{SQRT}[\text{H2O}(\text{Pa}/760)(298/\text{Ta})]$ | | | y axis = $\text{SQRT}[\text{H2O}(\text{Ta}/\text{Pa})]$ | | |

CALCULATIONS

$V_{std} = \text{Diff. Vol} [(\text{Pa} - \text{Diff. Hg}) / 760] (298 / \text{Ta})$
 $Q_{std} = V_{std} / \text{Time}$

$V_a = \text{Diff Vol} [(\text{Pa} - \text{Diff Hg}) / \text{Pa}]$
 $Q_a = V_a / \text{Time}$

For subsequent flow rate calculations:

$Q_{std} = 1/m \{ [\text{SQRT}(\text{H2O}(\text{Pa}/760)(298/\text{Ta}))] - b \}$
 $Q_a = 1/m \{ [\text{SQRT}(\text{H2O}(\text{Ta}/\text{Pa}))] - b \}$



Certificate of Calibration 校正證書

Certificate No. : C142871
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC14-0853) Date of Receipt / 收件日期 : 8 May 2014
Description / 儀器名稱 : Integrating Sound Level Meter (EQ006)
Manufacturer / 製造商 : Brüel & Kjær
Model No. / 型號 : 2238
Serial No. / 編號 : 2285762
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C Relative Humidity / 相對濕度 : (55 ± 20)%
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 13 May 2014


TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By : 
測試 : K C Lee
Project Engineer

Certified By : 
核證 : K M Wu
Engineer

Date of Issue : 15 May 2014
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Certificate of Calibration

校正證書

Certificate No. : C142871
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration using laboratory acoustic calibrator was performed before the test from 6.1.1.2 to 6.4.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

| Equipment ID | Description | Certificate No. |
|--------------|-------------------------------------|-----------------|
| CL280 | 40 MHz Arbitrary Waveform Generator | C140016 |
| CL281 | Multifunction Acoustic Calibrator | DC130171 |

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

6.1.1.1 Before Self-calibration

| UUT Setting | | | | Applied Value | | UUT Reading (dB) |
|-------------|------------------|---------------------|----------------|---------------|-------------|------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. (kHz) | |
| 50 - 130 | L _{AFP} | A | F | 94.00 | 1 | 94.3 |

6.1.1.2 After Self-calibration

| UUT Setting | | | | Applied Value | | UUT Reading (dB) | IEC 60651 Type 1 Spec. (dB) |
|-------------|------------------|---------------------|----------------|---------------|-------------|------------------|-----------------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. (kHz) | | |
| 50 - 130 | L _{AFP} | A | F | 94.00 | 1 | 94.0 | ± 0.7 |

6.1.2 Linearity

| UUT Setting | | | | Applied Value | | UUT Reading (dB) |
|-------------|------------------|---------------------|----------------|---------------|-------------|------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. (kHz) | |
| 50 - 130 | L _{AFP} | A | F | 94.00 | 1 | 94.0 (Ref.) |
| | | | | 104.00 | | 104.0 |
| | | | | 114.00 | | 113.9 |

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C142871

證書編號

6.2 Time Weighting

6.2.1 Continuous Signal

| UUT Setting | | | | Applied Value | | UUT Reading (dB) | IEC 60651 Type 1 Spec. (dB) |
|-------------|------------------|---------------------|----------------|---------------|-------------|------------------|-----------------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. (kHz) | | |
| 50 - 130 | L _{AFP} | A | F | 94.00 | 1 | 94.0 | Ref. |
| | L _{ASP} | | S | | | 94.0 | ± 0.1 |
| | L _{AIP} | | I | | | 94.0 | ± 0.1 |

6.2.2 Tone Burst Signal (2 kHz)

| UUT Setting | | | | Applied Value | | UUT Reading (dB) | IEC 60651 Type 1 Spec. (dB) |
|-------------|--------------------|---------------------|----------------|---------------|----------------|------------------|-----------------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Burst Duration | | |
| 30 - 110 | L _{AFP} | A | F | 106.0 | Continuous | 106.0 | Ref. |
| | L _{AFMax} | | | | 200 ms | 105.0 | -1.0 ± 1.0 |
| | L _{ASP} | S | Continuous | | 106.0 | Ref. | |
| | L _{ASMax} | | 500 ms | | 102.0 | -4.1 ± 1.0 | |

6.3 Frequency Weighting

6.3.1 A-Weighting

| UUT Setting | | | | Applied Value | | UUT Reading (dB) | IEC 60651 Type 1 Spec. (dB) |
|-------------|------------------|---------------------|----------------|---------------|----------|------------------|-----------------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. | | |
| 50 - 130 | L _{AFP} | A | F | 94.00 | 31.5 Hz | 55.1 | -39.4 ± 1.5 |
| | | | | | 63 Hz | 68.0 | -26.2 ± 1.5 |
| | | | | | 125 Hz | 77.9 | -16.1 ± 1.0 |
| | | | | | 250 Hz | 85.3 | -8.6 ± 1.0 |
| | | | | | 500 Hz | 90.8 | -3.2 ± 1.0 |
| | | | | | 1 kHz | 94.0 | Ref. |
| | | | | | 2 kHz | 95.2 | +1.2 ± 1.0 |
| | | | | | 4 kHz | 95.0 | +1.0 ± 1.0 |
| | | | | | 8 kHz | 92.9 | -1.1 (+1.5 ; -3.0) |
| | | | | | 12.5 kHz | 89.8 | -4.3 (+3.0 ; -6.0) |

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C142871
證書編號

6.3.2 C-Weighting

| UUT Setting | | | | Applied Value | | UUT Reading (dB) | IEC 60651 Type 1 Spec. (dB) |
|-------------|------------------|---------------------|----------------|---------------|----------|------------------|-----------------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. | | |
| 50 - 130 | L _{CFP} | C | F | 94.00 | 31.5 Hz | 91.4 | -3.0 ± 1.5 |
| | | | | | 63 Hz | 93.3 | -0.8 ± 1.5 |
| | | | | | 125 Hz | 93.8 | -0.2 ± 1.0 |
| | | | | | 250 Hz | 94.0 | 0.0 ± 1.0 |
| | | | | | 500 Hz | 94.0 | 0.0 ± 1.0 |
| | | | | | 1 kHz | 94.0 | Ref. |
| | | | | | 2 kHz | 93.8 | -0.2 ± 1.0 |
| | | | | | 4 kHz | 93.2 | -0.8 ± 1.0 |
| | | | | | 8 kHz | 91.0 | -3.0 (+1.5 ; -3.0) |
| | | | | | 12.5 kHz | 87.8 | -6.2 (+3.0 ; -6.0) |

6.4 Time Averaging

| UUT Setting | | | | Applied Value | | | | | UUT Reading (dB) | IEC 60804 Type 1 Spec. (dB) | |
|-------------|------------------|---------------------|------------------|-----------------|---------------------|-------------------|------------------|-----------------------|------------------|-----------------------------|-------|
| Range (dB) | Parameter | Frequency Weighting | Integrating Time | Frequency (kHz) | Burst Duration (ms) | Burst Duty Factor | Burst Level (dB) | Equivalent Level (dB) | | | |
| 30 - 110 | L _{Aeq} | A | 10 sec. | 4 | 1 | 1/10 | 110.0 | 100 | 99.9 | ± 0.5 | |
| | | | | | | | | 90 | 89.5 | ± 0.5 | |
| | | | 60 sec. | | | | | 1/10 ³ | 80 | 79.2 | ± 1.0 |
| | | | 5 min. | | | | | 1/10 ⁴ | 70 | 69.1 | ± 1.0 |

Remarks : - UUT Microphone Model No. : 4188 & S/N : 2812705

- Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :

| | |
|--------------------------|---|
| 94 dB : 31.5 Hz - 125 Hz | : ± 0.35 dB |
| 250 Hz - 500 Hz | : ± 0.30 dB |
| 1 kHz | : ± 0.20 dB |
| 2 kHz - 4 kHz | : ± 0.35 dB |
| 8 kHz | : ± 0.45 dB |
| 12.5 kHz | : ± 0.70 dB |
| 104 dB : 1 kHz | : ± 0.10 dB (Ref. 94 dB) |
| 114 dB : 1 kHz | : ± 0.10 dB (Ref. 94 dB) |
| Burst equivalent level | : ± 0.2 dB (Ref. 110 dB continuous sound level) |

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。



Certificate of Calibration 校正證書

Certificate No. : C142872
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC14-0853) Date of Receipt / 收件日期 : 8 May 2014
Description / 儀器名稱 : Integrating Sound Level Meter (EQ008)
Manufacturer / 製造商 : Brüel & Kjær
Model No. / 型號 : 2238
Serial No. / 編號 : 2285690
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C Relative Humidity / 相對濕度 : (55 ± 20)%
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範


Calibration check


DATE OF TEST / 測試日期 : 13 May 2014

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :
- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By : 
測試 : K C Lee
Project Engineer

Certified By : 
核證 : K M Wu
Engineer

Date of Issue : 15 May 2014
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C142872
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration using laboratory acoustic calibrator was performed before the test from 6.1.1.2 to 6.4.
- The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment :

| Equipment ID | Description | Certificate No. |
|--------------|-------------------------------------|-----------------|
| CL280 | 40 MHz Arbitrary Waveform Generator | C140016 |
| CL281 | Multifunction Acoustic Calibrator | DC130171 |

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

6.1.1.1 Before Self-calibration

| UUT Setting | | | | Applied Value | | UUT Reading (dB) |
|-------------|------------------|---------------------|----------------|---------------|-------------|------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. (kHz) | |
| 50 - 130 | L _{AFP} | A | F | 94.00 | 1 | 94.2 |

6.1.1.2 After Self-calibration

| UUT Setting | | | | Applied Value | | UUT Reading (dB) | IEC 60651 Type 1 Spec. (dB) |
|-------------|------------------|---------------------|----------------|---------------|-------------|------------------|-----------------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. (kHz) | | |
| 50 - 130 | L _{AFP} | A | F | 94.00 | 1 | 94.1 | ± 0.7 |

6.1.2 Linearity

| UUT Setting | | | | Applied Value | | UUT Reading (dB) |
|-------------|------------------|---------------------|----------------|---------------|-------------|------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. (kHz) | |
| 50 - 130 | L _{AFP} | A | F | 94.00 | 1 | 94.1 (Ref.) |
| | | | | 104.00 | | 104.1 |
| | | | | 114.00 | | 114.0 |

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C142872
證書編號

6.2 Time Weighting

6.2.1 Continuous Signal

| UUT Setting | | | | Applied Value | | UUT Reading (dB) | IEC 60651 Type 1 Spec. (dB) |
|-------------|------------------|---------------------|----------------|---------------|-------------|------------------|-----------------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. (kHz) | | |
| 50 - 130 | L _{AFP} | A | F | 94.00 | 1 | 94.1 | Ref. |
| | L _{ASP} | | S | | | 94.1 | ± 0.1 |
| | L _{AIP} | | I | | | 94.1 | ± 0.1 |

6.2.2 Tone Burst Signal (2 kHz)

| UUT Setting | | | | Applied Value | | UUT Reading (dB) | IEC 60651 Type 1 Spec. (dB) |
|-------------|--------------------|---------------------|----------------|---------------|----------------|------------------|-----------------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Burst Duration | | |
| 30 - 110 | L _{AFP} | A | F | 106.0 | Continuous | 106.0 | Ref. |
| | L _{AFMax} | | | | 200 ms | 105.0 | -1.0 ± 1.0 |
| | L _{ASP} | | S | | Continuous | 106.0 | Ref. |
| | L _{ASMax} | | | | 500 ms | 102.0 | -4.1 ± 1.0 |

6.3 Frequency Weighting

6.3.1 A-Weighting

| UUT Setting | | | | Applied Value | | UUT Reading (dB) | IEC 60651 Type 1 Spec. (dB) |
|-------------|------------------|---------------------|----------------|---------------|---------|------------------|-----------------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. | | |
| 50 - 130 | L _{AFP} | A | F | 94.00 | 31.5 Hz | 54.8 | -39.4 ± 1.5 |
| | | | | | 63 Hz | 67.9 | -26.2 ± 1.5 |
| | | | | | 125 Hz | 77.9 | -16.1 ± 1.0 |
| | | | | | 250 Hz | 85.4 | -8.6 ± 1.0 |
| | | | | | 500 Hz | 90.8 | -3.2 ± 1.0 |
| | | | | | 1 kHz | 94.1 | Ref. |
| | | | | | 2 kHz | 95.3 | +1.2 ± 1.0 |
| | | | | | 4 kHz | 95.1 | +1.0 ± 1.0 |
| | | | | | 8 kHz | 93.0 | -1.1 (+1.5 ; -3.0) |
| 12.5 kHz | 89.9 | -4.3 (+3.0 ; -6.0) | | | | | |

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C142872
證書編號

6.3.2 C-Weighting

| UUT Setting | | | | Applied Value | | UUT Reading (dB) | IEC 60651 Type 1 Spec. (dB) |
|-------------|------------------|---------------------|----------------|---------------|----------|------------------|-----------------------------|
| Range (dB) | Parameter | Frequency Weighting | Time Weighting | Level (dB) | Freq. | | |
| 50 - 130 | L _{CFP} | C | F | 94.00 | 31.5 Hz | 91.2 | -3.0 ± 1.5 |
| | | | | | 63 Hz | 93.3 | -0.8 ± 1.5 |
| | | | | | 125 Hz | 93.9 | -0.2 ± 1.0 |
| | | | | | 250 Hz | 94.1 | 0.0 ± 1.0 |
| | | | | | 500 Hz | 94.1 | 0.0 ± 1.0 |
| | | | | | 1 kHz | 94.1 | Ref. |
| | | | | | 2 kHz | 93.9 | -0.2 ± 1.0 |
| | | | | | 4 kHz | 93.3 | -0.8 ± 1.0 |
| | | | | | 8 kHz | 91.1 | -3.0 (+1.5 ; -3.0) |
| | | | | | 12.5 kHz | 88.0 | -6.2 (+3.0 ; -6.0) |

6.4 Time Averaging

| UUT Setting | | | | Applied Value | | | | | UUT Reading (dB) | IEC 60804 Type 1 Spec. (dB) | |
|-------------|------------------|---------------------|------------------|-----------------|---------------------|-------------------|------------------|-----------------------|------------------|-----------------------------|-------|
| Range (dB) | Parameter | Frequency Weighting | Integrating Time | Frequency (kHz) | Burst Duration (ms) | Burst Duty Factor | Burst Level (dB) | Equivalent Level (dB) | | | |
| 30 - 110 | L _{Aeq} | A | 10 sec. | 4 | 1 | 1/10 | 110.0 | 100 | 99.9 | ± 0.5 | |
| | | | | | | | | 90 | 89.7 | ± 0.5 | |
| | | | 60 sec. | | | | | 1/10 ³ | 80 | 79.8 | ± 1.0 |
| | | | 5 min. | | | | | 1/10 ⁴ | 70 | 69.8 | ± 1.0 |

Remarks : - UUT Microphone Model No. : 4188 & S/N : 2812706

- Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :

| | |
|--------------------------|---|
| 94 dB : 31.5 Hz - 125 Hz | : ± 0.35 dB |
| 250 Hz - 500 Hz | : ± 0.30 dB |
| 1 kHz | : ± 0.20 dB |
| 2 kHz - 4 kHz | : ± 0.35 dB |
| 8 kHz | : ± 0.45 dB |
| 12.5 kHz | : ± 0.70 dB |
| 104 dB : 1 kHz | : ± 0.10 dB (Ref. 94 dB) |
| 114 dB : 1 kHz | : ± 0.10 dB (Ref. 94 dB) |
| Burst equivalent level | : ± 0.2 dB (Ref. 110 dB continuous sound level) |

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Appendix E

HOKLAS-Accreditation Certificate of the Testing Laboratory



Hong Kong Accreditation Service
香港認可處

Certificate of Accreditation
認可證書

This is to certify that
特此證明

ALS TECHNICHEM (HK) PTY LIMITED

11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong
香港新界葵涌永業街1-3號忠信針織中心11樓

has been accepted by the HKAS Executive, on the recommendation of the Accreditation Advisory Board, as a
為香港認可處執行機關根據認可諮詢委員會建議而接受的

HOKLAS Accredited Laboratory
「香港實驗所認可計劃」認可實驗所

This laboratory meets the requirements of ISO / IEC 17025 : 2005 – General requirements for the competence of testing and calibration laboratories and it has been accredited for performing specific tests or calibrations as listed in the HOKLAS Directory of Accredited Laboratories within the test category of
此實驗所符合ISO / IEC 17025 : 2005 –《測試及校正實驗所能力的通用規定》所訂的要求，獲認可進行載於香港實驗所認可計劃《認可實驗所名冊》內下述測試類別中的指定
測試或校正工作

Environmental Testing
環境測試

This laboratory is accredited in accordance with the recognised International Standard ISO / IEC 17025 : 2005.
本實驗所乃根據公認的國際標準 ISO / IEC 17025 : 2005 獲得認可。

This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (see joint IAF-ILAC-ISO Communiqué).
這項認可資格演示在指定範疇所需的技術能力及實驗所質量管理體系的運作
(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of the Hong Kong Accreditation Service is affixed hereto by the authority of the HKAS Executive
香港認可處根據認可處執行機關的權限在此蓋上通用印章

CHAN Sing Sing, Terence, Executive Administrator
執行幹事 陳成城
Issue Date : 5 May 2009
簽發日期：二零零九年五月五日

Registration Number : **HOKLAS 066**
註冊號碼：

Date of First Registration : 15 September 1995
首次註冊日期：一九九五年九月十五日



Appendix F

Event and Action Plan

Event and Action Plan for Construction Noise

| Event | Action | | | |
|--------------|--|--|--|--|
| | ET | IEC | ER | Contractor |
| Action Level | <ol style="list-style-type: none"> 1. Notify IEC and Contractor. 2. Carry out investigation. 3. Report the results of investigation to the IEC and Contractor. 4. Discuss with the Contractor and formulate remedial measures 5. Increase monitoring frequency to check mitigation effectiveness. | <ol style="list-style-type: none"> 1. Review the analyzed result submitted by ET. 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly. 3. Supervise the implementation of remedial measures. | <ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance 2. Notify Contractor 3. Require Contractor to propose remedial measures for the analyzed noise problem 4. Ensure remedial measures are properly implemented. | <ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC 2. Implement noise mitigation proposals |
| Limit Level | <ol style="list-style-type: none"> 1. Notify IEC, ER, EPD and Contractor, and follow other actions 2. Identify source 3. Repeat measurement to confirm findings 4. Increase monitoring frequency 5. Check Contractor's working procedures to determine possible mitigation to be implemented 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD, ER informed of the results 8. If exceedance stops, cease additional monitoring | <ol style="list-style-type: none"> 1. Discuss amongst ER, ET and Contractor on the potential remedial actions 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ET accordingly 3. Supervise the implementation of remedial measures | <ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedances 2. Notify Contractor 3. Require Contractor to propose remedial measures 4. Ensure remedial measures are properly implemented 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. | <ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance 2. Submit proposals for remedial actions to IEC within 3 working days of notifications 3. Implement the agreed proposals 4. Revise and resubmit proposals if problem still not under control 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated |

Event and Action Plan for Air Quality

| Event | Action | | | |
|--|--|---|---|---|
| | ET | IEC | ER | Contractor |
| Action Level | | | | |
| Exceedance for one sample | 1. Identify source; 2. If valid, inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily | 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. | 1. Notify Contractor | 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate |
| Exceedance for two or more consecutive samples | 1. Identify source; 2. Inform IEC and EPD; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency to daily; 5. Discuss with IEC and Contractor on remedial action required; 6. If exceedance continues, arrange meeting with IEC and ER; 7. If exceedance stops, cease additional monitoring. | 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervisor implementation of remedial measures. | 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial Measure properly implemented. | 1. Submit proposals for remedial action to IEC within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate. |
| Limit Level | | | | |
| Exceedance for one sample | 1. Identify source; 2. Inform ER and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. | 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and the Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. | 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. | 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate. |
| Exceedance for two or more consecutive samples | 1. Notify IEC, ER, Contractor and EPD; 2. Identify sources; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops cease additional monitoring. | 1. Discuss amongst ER, ET and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ET accordingly. 3. Supervise the implementation of remedial measures. | 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated | 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated. |

Appendix G

Monitoring Schedule

Monitoring Schedule in the Reporting Period (28 August 2014 – 30 September 2014)

| Date | | Air Quality | Noise |
|------|-----------|-------------|----------|
| | | 24-hour TSP | Leq30min |
| Thu | 28-Aug-14 | ✓ | |
| Fri | 29-Aug-14 | | |
| Sat | 30-Aug-14 | | |
| Sun | 31-Aug-14 | | |
| Mon | 1-Sep-14 | | |
| Tue | 2-Sep-14 | | |
| Wed | 3-Sep-14 | ✓ | ✓ |
| Thu | 4-Sep-14 | | |
| Fri | 5-Sep-14 | | |
| Sat | 6-Sep-14 | | |
| Sun | 7-Sep-14 | | |
| Mon | 8-Sep-14 | ✓ | |
| Tue | 9-Sep-14 | | |
| Wed | 10-Sep-14 | | ✓ |
| Thu | 11-Sep-14 | | |
| Fri | 12-Sep-14 | | |
| Sat | 13-Sep-14 | ✓ | |
| Sun | 14-Sep-14 | | |
| Mon | 15-Sep-14 | | ✓ |
| Tue | 16-Sep-14 | | |
| Wed | 17-Sep-14 | | |
| Thu | 18-Sep-14 | | |
| Fri | 19-Sep-14 | ✓ | |
| Sat | 20-Sep-14 | | |
| Sun | 21-Sep-14 | | |
| Mon | 22-Sep-14 | | ✓ |
| Tue | 23-Sep-14 | | |
| Wed | 24-Sep-14 | | |
| Thu | 25-Sep-14 | ✓ | |
| Fri | 26-Sep-14 | | |
| Sat | 27-Sep-14 | | |
| Sun | 28-Sep-14 | | |
| Mon | 29-Sep-14 | | ✓ |
| Tue | 30-Sep-14 | ✓ | |

Air Quality Monitoring Location

A1 - balcony at 1/F of Chiu Hin Mansion

Construction Noise Monitoring Location:

N1 - 2/F floor of Hennessey Building

N2 - balcony at 1/F of Chiu Hin Mansion

Monitoring Schedule for the Coming Month – October 2014

| Date | | Air Quality | Noise |
|------|-----------|-------------|----------|
| | | 24-hour TSP | Leq30min |
| Wed | 1-Oct-14 | | |
| Thu | 2-Oct-14 | | |
| Fri | 3-Oct-14 | | |
| Sat | 4-Oct-14 | | |
| Sun | 5-Oct-14 | | |
| Mon | 6-Oct-14 | | |
| Tue | 7-Oct-14 | | |
| Wed | 8-Oct-14 | | ✓ |
| Thu | 9-Oct-14 | ✓ | |
| Fri | 10-Oct-14 | | |
| Sat | 11-Oct-14 | | |
| Sun | 12-Oct-14 | | |
| Mon | 13-Oct-14 | | |
| Tue | 14-Oct-14 | | |
| Wed | 15-Oct-14 | | ✓ |
| Thu | 16-Oct-14 | ✓ | |
| Fri | 17-Oct-14 | | |
| Sat | 18-Oct-14 | | |
| Sun | 19-Oct-14 | | |
| Mon | 20-Oct-14 | | ✓ |
| Tue | 21-Oct-14 | ✓ | |
| Wed | 22-Oct-14 | | |
| Thu | 23-Oct-14 | | |
| Fri | 24-Oct-14 | | |
| Sat | 25-Oct-14 | | |
| Sun | 26-Oct-14 | | |
| Mon | 27-Oct-14 | | ✓ |
| Tue | 28-Oct-14 | ✓ | |
| Wed | 29-Oct-14 | | |
| Thu | 30-Oct-14 | | |
| Fri | 31-Oct-14 | | |

Air Quality Monitoring Location

A1 - balcony at 1/F of Chiu Hin Mansion

Construction Noise Monitoring Location:

N1 - 2/F floor of Hennessey Building

N2 - balcony at 1/F of Chiu Hin Mansion

Appendix H

Database of Monitoring Results


Result of 24-hour TSP Monitoring

| Location: A1 (balcony at 1/F of Chiu Hin Mansion) | | | | | | | | | | | | | | | |
|--|---------------|--------------|----------|--------------|---------------|-----|------|-----------------|-------------------|---------------------------------|----------------------------------|-------------------|--------|---------------------------|--|
| Date | Sample Number | Elapsed Time | | | Chart Reading | | | Ave. Temp. (°C) | Standard | | | Filter Weight (g) | | Weight Dust Collected (g) | Dust 24-hour TSP in Air (µg/m ³) |
| | | Initial | Final | Actual (min) | Min | Max | Ave | | Ave. Press. (hPa) | Flow Rate (m ³ /min) | Air Volume (std m ³) | Initial | Final | | |
| 28-Aug-14 | 27080 | 15203.02 | 15227.43 | 1464.60 | 40 | 40 | 40.0 | 28.5 | 1006.0 | 1.32 | 1934 | 2.8137 | 2.8645 | 0.0508 | 26 |
| 3-Sep-14 | 208316 | 15227.43 | 15251.63 | 1452.00 | 39 | 40 | 39.5 | 28.5 | 1006.6 | 1.31 | 1895 | 2.7044 | 2.8523 | 0.1479 | 78 |
| 8-Sep-14 | 208348 | 15251.63 | 15275.73 | 1446.00 | 28 | 30 | 29.0 | 28.1 | 1007.8 | 0.97 | 1409 | 2.8434 | 2.8765 | 0.0331 | 24 |
| 13-Sep-14 | 208352 | 15275.73 | 15299.74 | 1440.60 | 39 | 40 | 39.5 | 27.9 | 1008.4 | 1.31 | 1884 | 2.8394 | 2.8834 | 0.0440 | 23 |
| 19-Sep-14 | 27162 | 15299.74 | 15323.76 | 1441.20 | 38 | 40 | 39.0 | 27.7 | 1009.5 | 1.29 | 1863 | 2.8135 | 3.0510 | 0.2375 | 127 |
| 25-Sep-14 | 27191 | 15323.76 | 15347.78 | 1441.20 | 39 | 40 | 39.5 | 27.1 | 1010.7 | 1.31 | 1889 | 2.8182 | 3.0292 | 0.2110 | 112 |
| 30-Sep-14 | 27192 | 15347.78 | 15371.91 | 1447.80 | 39 | 40 | 39.5 | 26.8 | 1011.8 | 1.31 | 1899 | 2.8280 | 3.0217 | 0.1937 | 102 |



Appendix I

Graphical Plots

Air Quality

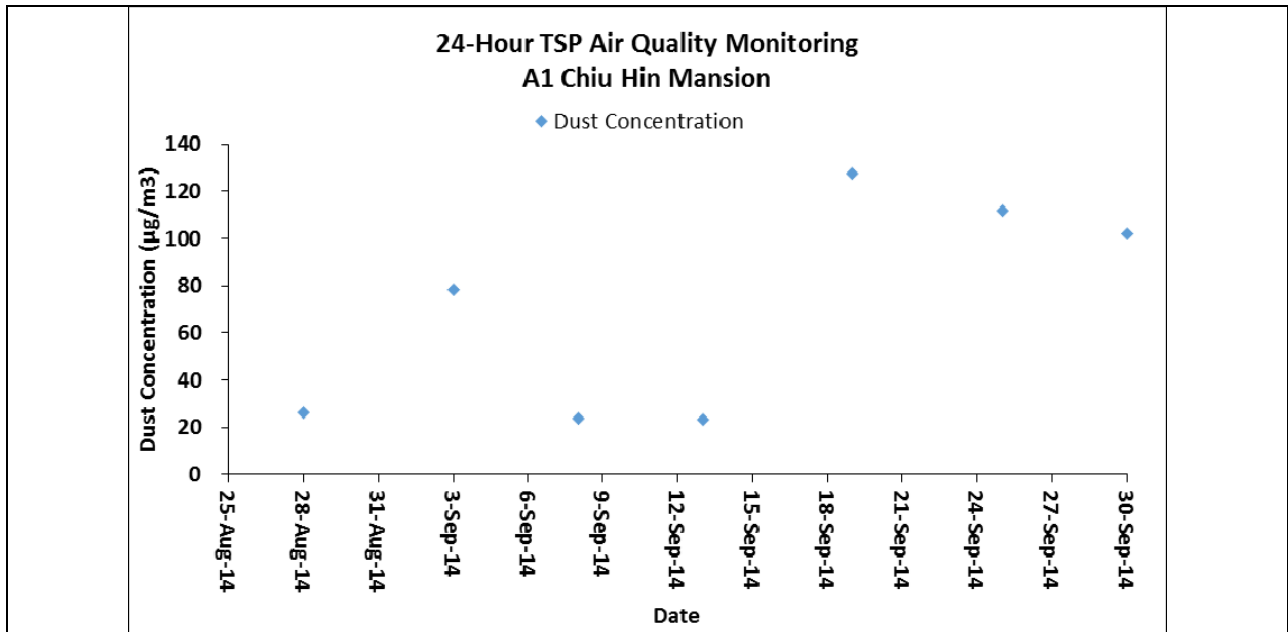

Construction Noise

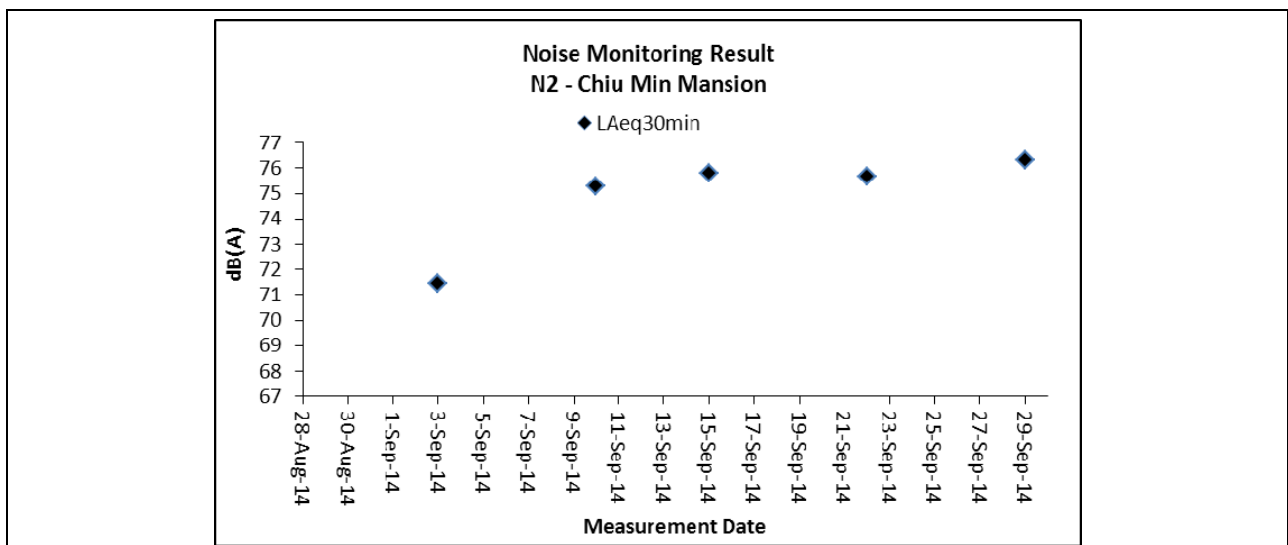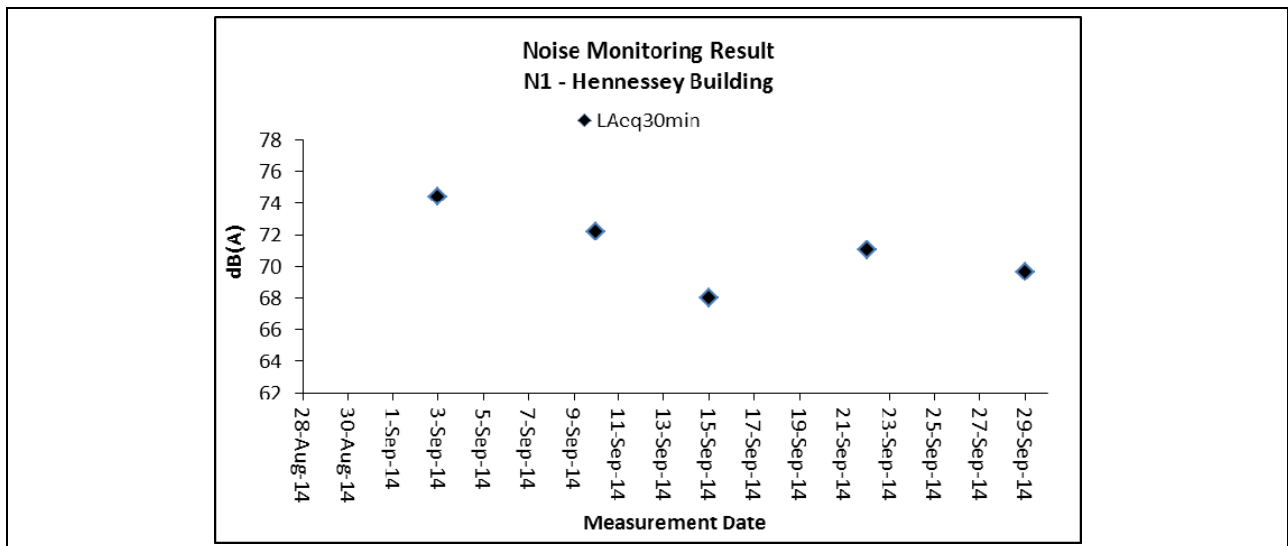

Appendix J

Meteorological Information

| Meteorological Data downloaded from HKO in the Reporting Period | | | | | | | |
|---|---------|---|---------------------|-------------------|----------------------------|----------------|------|
| Date | Weather | Total Rainfall (mm) | Kings Park Station | | | | |
| | | | Mean Air Temp. (°C) | Wind Speed (km/h) | Mean Relative Humidity (%) | Wind Direction | |
| 28-Aug-14 | Thu | Mainly fine and very hot, apart from isolated showers at first. Moderate east to southeasterly winds. | 0.3 | 29.4 | 16.1 | 80 | E/SE |
| 29-Aug-14 | Fri | Mainly fine and very hot, apart from isolated showers at first. Moderate east to southeasterly winds. | 0 | 29.6 | 7.2 | 73.7 | E/SE |
| 30-Aug-14 | Sat | Mainly fine and very hot, apart from isolated showers at first. Moderate east to southeasterly winds. | 0 | 29.9 | 8.9 | 72.5 | E/SE |
| 31-Aug-14 | Sun | Mainly fine and very hot, apart from isolated showers at first. Moderate east to southeasterly winds. | 1.6 | 29 | 9.5 | 81.7 | E/SE |
| 1-Sep-14 | Mon | Mainly fine. It will be very hot in the afternoon. Light to moderate southerly winds. | 2.2 | 29.7 | 8.4 | 80 | E/SE |
| 2-Sep-14 | Tue | Mainly fine. It will be very hot in the afternoon. Light to moderate southerly winds. | 0 | 29.2 | 7.5 | 73.7 | W/NW |
| 3-Sep-14 | Wed | Fine and very hot. Light to moderate westerly winds. | 0 | 29.9 | 8.3 | 72.5 | W/NW |
| 4-Sep-14 | Thu | Mainly fine at first. One or two showers and thunderstorms later. It will be hot. Light to moderate westerly winds. | 6.7 | 29.1 | 11 | 78 | W/NW |
| 5-Sep-14 | Fri | Mainly fine at first. One or two showers and thunderstorms later. It will be hot. Light to moderate westerly winds. | Trace | 29 | 7.8 | 81.7 | E/SE |
| 6-Sep-14 | Sat | Fine and very hot. Light to moderate westerly winds. | Trace | 29.9 | 7.3 | 75 | E/SE |
| 7-Sep-14 | Sun | Mainly cloudy with a few showers and isolated thunderstorms. Moderate to fresh east to southeasterly winds. | 0.6 | 29.6 | 11.6 | 79 | E/SE |
| 8-Sep-14 | Mon | Mainly cloudy with a few showers and isolated thunderstorms. Moderate to fresh southeasterly winds. | 3 | 28.9 | 8 | 82 | S/SE |
| 9-Sep-14 | Tue | Mainly fine apart from isolated showers. Very hot. Light to moderate south to southeasterly winds. | 0 | 30 | 7.5 | 74.7 | W/NW |
| 10-Sep-14 | Wed | Mainly fine apart from isolated showers. Very hot. Light to moderate east to southeasterly winds. | Trace | 30.2 | 5 | 70.7 | W/NW |
| 11-Sep-14 | Thu | Mainly fine and very hot apart from isolated showers. Light to moderate east to southeasterly winds. | Trace | 30.2 | 7.2 | 74.5 | SE |
| 12-Sep-14 | Fri | Mainly fine apart from isolated showers. Very hot. Light to moderate east to southeasterly winds. | 32.1 | 28.1 | 10 | 84 | E/SE |
| 13-Sep-14 | Sat | Mainly fine and very hot apart from isolated showers. Light to moderate east to southeasterly winds. | 6.2 | 29.4 | 8.2 | 81 | E/SE |
| 14-Sep-14 | Sun | Mainly fine apart from isolated showers. Very hot. Light to moderate east to southeasterly winds. | 0.5 | 30 | 7.5 | 76.5 | E/SE |
| 15-Sep-14 | Mon | Cloudy to overcast with heavy squally showers and a few thunderstorms. | 17.6 | 29.1 | 18.7 | 77.2 | E/NE |
| 16-Sep-14 | Tue | Strong southeasterly winds. Seas will be rough with swells. Cloudy with heavy squally showers and thunderstorms. | 51.6 | 27.1 | 30.5 | 85 | SE |
| 17-Sep-14 | Wed | Mainly cloudy with a few showers. Sunny intervals. Moderate to fresh southeasterly winds, strong offshore at first. | 7.7 | 27.7 | 12.6 | 89.2 | S/SE |
| 18-Sep-14 | Thu | Mainly fine and hot. Light to moderate southeasterly winds. | Trace | 29 | 6.5 | 79.5 | W/NW |
| 19-Sep-14 | Fri | Fine and very hot apart from some haze. Isolated showers later. Light to moderate northerly winds. | 0.3 | 29.7 | 7.2 | 78 | W |
| 20-Sep-14 | Sat | Fine and very hot apart from some haze. Isolated showers later. Light to moderate northerly winds. | 0 | 28.9 | 9.4 | 66.5 | N/NE |
| 21-Sep-14 | Sun | Mainly fine and dry. Light to moderate north to northeasterly winds. | 0 | 27.2 | 7.6 | 65 | N/NE |
| 22-Sep-14 | Mon | Mainly fine and dry. Light to moderate north to northeasterly winds. | Trace | 27.5 | 6.1 | 62.2 | N/NE |
| 23-Sep-14 | Tue | Mainly fine. Dry in the afternoon. Light to moderate north to northeasterly winds. | 0 | 27.9 | 4.5 | 67.2 | NE |
| 24-Sep-14 | Wed | Mainly cloudy with isolated showers. Light to moderate northerly winds. | 0 | 28 | 4 | 76.2 | W/NW |
| 25-Sep-14 | Thu | Sunny periods with haze. Isolated showers in the afternoon. Mainly cloudy tonight. Light winds | 0 | 28.2 | 5.3 | 77.2 | W/NW |
| 26-Sep-14 | Fri | Mainly cloudy with isolated showers. Sunny intervals in the afternoon. Light to moderate easterly winds. | 0.7 | 28.7 | 6 | 76 | E/SE |
| 27-Sep-14 | Sat | Mainly cloudy with isolated showers. Sunny intervals in the afternoon. Light to moderate easterly winds. | 0 | 29.2 | 7 | 75 | SE |
| 28-Sep-14 | Sun | Mainly cloudy with isolated showers. Light to moderate northerly winds. | 0 | 29 | 6 | 73.5 | SE |
| 29-Sep-14 | Mon | Mainly fine. Dry in the afternoon. Light to moderate north to northeasterly winds. | 0 | 29.2 | 5.3 | 73 | W |
| 30-Sep-14 | Tue | Cloudy with showers and a few squally thunderstorms. Moderate easterly winds, fresh at time | 11.4 | 30.1 | 4.8 | 76 | W/NW |

Appendix K

Monthly Summary Waste Flow Table

Wan Chai Station Lee Tung Street Subway- C6593-13C

Monthly Summary Waste Flow Table for 2014

| Name of Employer: MTR Corporation Limited | | | | | | | | | | | Contract No.: C65931-13C | | | | |
|---|--|-----------------|-----------------|-------------------|-----------|----------|----------|----------|--------------|------------------------|---|----------------------------|----------|------------------|-----------------------------|
| Month | Actual Quantities of Inert C&D Materials Generated Monthly | | | | | | | | | | Actual Quantities of Non-Inert C&D Wastes Generated Monthly | | | | |
| | Total Quantity Generated | Broken Concrete | Building Debris | Mixed Rock & Soil | Bentonite | Rubbish | Slurry | Rock | Soil | Reused in this Project | Metals | Paper/ cardboard packaging | Plastics | Chemical Waste | Others, e.g. general refuse |
| | (in ton) | (in ton) | (in ton) | (in ton) | (in ton) | (in ton) | (in ton) | (in ton) | (in ton) | (in ton) | (in ton) | (in ton) | (in ton) | (in ton / Litre) | (in ton) |
| Jan | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| Feb | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| Mar | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| Apr | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| May | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| Jun | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| Jul | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| Aug | 15.81 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 15.81 | 0 | 0 | 0 | 0 | 0 | 0 |
| Sep | 39.67 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 39.67 | 0 | 0 | 0 | 0 | 0 | 0.67 |
| Oct | | | | | | | | | | | | | | | |
| Nov | | | | | | | | | | | | | | | |
| Dec | | | | | | | | | | | | | | | |
| Total | 55.48 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 55.48 | 0 | 0 | 0 | 0 | 0 | 0.67 |

Notes:

Appendix L

Implementation Schedule for Environmental Mitigation Measures (ISEMM)

| Project Profile Ref. | Recommended Mitigation Measures | Objectives of the Recommended Measures & Main Concerns to address | Implementation Parties | Location of the measure | When to implement the measure | Relevant requirements or standards for the measure to achieve |
|----------------------|---|---|------------------------|-------------------------|-------------------------------|---|
| NOISE IMPACT | | | | | | |
| S.5.1.1 | <u>Use of quieter plant</u> | To minimize construction noise emissions | Contractor | Work site | Construction Stage | ProPECC PN2/93 and Noise Control Ordinance |
| S.5.1.1 | <p><u>Use of noise enclosure and movable barrier</u></p> <ul style="list-style-type: none"> • movable barrier can achieve a 5 dB(A) reduction for movable PME and 10 dB(A) reduction for stationary PME; • noise enclosure can achieve 15dB(A) reduction for PME; • noise enclosure is proposed to be built after open excavation in order to minimize the noise impact due to further excavation work and construction of subway. The enclosure should either be provided with acoustic door for access purpose which should be kept closed during the construction works or should be designed with no direct line of sight from the open side to the NSRs; • A typical design barrier with a steel frame of vertical / cantilever type would be adopted and located close to the noise generating part of PME; • Barrier material of surface mass in excess of 7kg/m² shall be required to achieve the maximum screening effect (and minimum 10kg/m² for noise enclosure); • The length of barrier should generally be at least five times greater than its height and the minimum height of a barrier should be such that no part of the noise source will be visible from the noise sensitive receiver being protected. | To minimize construction noise emissions | Contractor | Work site | Construction Stage | ProPECC PN2/93, Noise Control Ordinance and EIAO Guidance Note NO. 9/2010 |
| S.5.1.1 | <p><u>General Construction Noise Control Measures</u></p> <ul style="list-style-type: none"> • The Code of Practice on Good Management Practice to Prevent Violation of the Noise Control Ordinance (Chapter 400) (for Construction Industry) published by EPD shall be adopted; • The statutory and non-statutory requirements and guidelines shall be complied with; • Approval for the method of working, equipment and noise mitigation measures intended to be used at the site shall be granted from the Project Engineer before commencing any work; | To minimize construction noise emissions | Contractor | Work site | Construction Stage | ProPECC PN2/93 and Noise Control Ordinance |

| Project Profile Ref. | Recommended Mitigation Measures | Objectives of the Recommended Measures & Main Concerns to address | Implementation Parties | Location of the measure | When to implement the measure | Relevant requirements or standards for the measure to achieve |
|---------------------------|--|---|------------------------|-------------------------|-------------------------------|---|
| | <ul style="list-style-type: none"> • Working methods to minimize the noise impact on the surrounding NSRs shall be formulated and executed, and the implementation of these methods shall be monitored by experienced personnel with suitable training; • Noisy equipment and noisy activities shall be located as far away from the NSRs as is practical; • Unused equipment shall be turned off; • PME should be kept to a minimum and the parallel use of noisy equipment / machinery should be avoided; • All plant and equipment shall be maintained regularly; and • Material stockpiles and other structures shall be effectively utilized as noise barriers, whenever practicable. | | | | | |
| AIR QUALITY IMPACT | | | | | | |
| S.5.1.2 | <p><u>Construction Dust Control Measures</u></p> <ul style="list-style-type: none"> • Regular watering to reduce dust emissions from all exposed site surface, particularly during dry weather; • Frequent watering for particularly dusty construction areas and areas close to air sensitive receivers; • Covering of stockpile of excavated dusty materials, if any, with impervious sheeting or spraying with water to maintain the entire surface wet; • Provision of vehicle washing facilities at the entry and exit points of site; • Tarpaulin covering of any dusty materials being transported to and from site by vehicle; • Positioning of construction plant at maximum practicable distance from air sensitive receivers; and • Due to the small size of the works sites and lack of space for stockpiling, excavated materials should be hauled off-site almost immediately. However, in the event of any stockpiled excavated materials, they should be covered with tarpaulin and be removed offsite as soon as practicable to avoid any dust nuisance arising | To minimize the dust impacts arising from the construction works | Contractor | Work site | Construction Stage | Air Pollution Control (Construction Dust) Regulation |

| Project Profile Ref. | Recommended Mitigation Measures | Objectives of the Recommended Measures & Main Concerns to address | Implementation Parties | Location of the measure | When to implement the measure | Relevant requirements or standards for the measure to achieve |
|-----------------------------|--|---|------------------------|-------------------------|-------------------------------|---|
| WATER QUALITY IMPACT | | | | | | |
| S.5.1.3 | <p><u>Construction Water Quality Impact Measures</u></p> <ul style="list-style-type: none"> • Collection of wastewater into a sedimentation tank for treatment before discharge into the public drainage system; • Provision of silt trap and oil interceptor to remove the oil, lubricants, grease, silt, grit and debris from the wastewater prior to discharge to the public stormwater system. The silt traps and oil interceptors should be cleaned and maintained regularly; • Installation of wheel washing facilities to minimize muddy runoff; • Regular maintenance and inspection of drainage systems and erosion control and silt removal facilities; • Management and monitoring of sewage treatment facilities (if any); • Any foul effluent should not be discharged into any public sewer and stormwater drain, unless an effluent discharge permit is obtained under the WPCO by the Contractor; • Coverage of stockpiles of C&D materials (if any) during rainstorms; and • Site toilet facilities, if needed, should be chemical toilets or should have the sewage discharge directed to a foul sewer. | To reduce water quality impact induced by the construction work | Contractor | Work site | Construction Stage | ProPECC PN1/94; Water Pollution Control Ordinance |
| WASTE MANAGEMENT | | | | | | |
| S.5.1.4 | <p><u>Construction Waste Management Measures</u></p> <ul style="list-style-type: none"> • Scrap metals or abandoned equipment should be recycled if possible; • Waste arising should be kept to a minimum and be handled, transported and disposed of in a suitable manner; • The Contractor should adopt a trip ticket system for the disposal of C&D materials to any designated public filling facility and/or landfill. Independent audits of the Contractor and resident site staff will be undertaken to ensure that the correct procedures are being followed; • Chemical waste shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes; and | To adopt waste management measures in the way of avoiding, minimizing, reusing and recycling so as to reduce waste generation | Contractor | Work site | Construction Stage | Waste Disposal Ordinance (Cap. 354); Waste Disposal (Chemical Waste) (General) Regulation; DEVB TCW No. 6/2010; ETWB TCW No. 19/2005. |

| Project Profile Ref. | Recommended Mitigation Measures | Objectives of the Recommended Measures & Main Concerns to address | Implementation Parties | Location of the measure | When to implement the measure | Relevant requirements or standards for the measure to achieve |
|------------------------------------|--|---|------------------------|---------------------------------|-------------------------------|---|
| | <ul style="list-style-type: none"> All general refuse should be segregated and stored in enclosed bins or compaction units and waste separation facilities for paper, aluminum cans, plastic bottles etc. should be provided to facilitate reuse or recycling of materials and their proper disposal. | | | | | |
| LANDSCAPE AND VISUAL IMPACT | | | | | | |
| S.5.1.5 | <p><u>Landscape and Visual Measures</u></p> <ul style="list-style-type: none"> Clear demarcation of works area to prevent damages to existing trees in close proximity; Protection of all trees planned to be retained onsite; Preserving all affected trees by transplanting where practical. Tree transplanting application and tree removal application shall be submitted for approval in accordance with ETWB TCW 3/2006; and Screening of construction works by hoardings/noise barriers around Works area in visually unobtrusive colours. | To reduce landscape and visual impact by construction works. | Contractor | Work Site and nearby playground | Construction Stage | EIAO; ETWB TCW No. 3/2006. |
