

Development at West Kowloon Cultural District

Monthly Environmental Monitoring and Audit (EM&A) Report for April 2019

May 2019

3/F Mapletree Bay Point 348 Kwun Tong Road Kwun Tong Kowloon Hong Kong

T +852 2828 5757 F +852 2827 1823 mottmac.hk

Development at West Kowloon Cultural District

Monthly Environmental Monitoring and Audit (EM&A) Report for April 2019

May 2019

This Monthly EM&A Report has been reviewed and certified by the Environmental Team Leader (ETL) and verified by the Independent Environmental Checker (IEC).

Certified by:

۲ Ì

Brian Tam Environmental Team Leader (ETL) West Kowloon Cultural District Authority

Date

14 May 2019

Verified by:

Fredrick Leong Independent Environmental Checker (IEC) Meinhardt Infrastructure & Environment Ltd

14 May 2019

Date

Contents

Ex	ecutiv	ve Summary	1
1	Intr	oduction	3
	1.1	Background	3
	1.2	Project Organisation	3
	1.3	Environmental Status in the Reporting Period	3
	1.4	Summary of EM&A Requirements	4
2	Imp	pact Monitoring Methodology	6
	2.1	Introduction	6
	2.2	Air Quality	6
		2.2.1 Monitoring Parameters, Frequency and Duration	6
		2.2.2 Monitoring Locations	6
		2.2.3 Monitoring Equipment	6
		2.2.4 Monitoring Methodology	7
	2.3	Noise	8
		2.3.1 Monitoring Parameters, Frequency and Duration	8
		2.3.2 Monitoring Location	9
		2.3.3 Monitoring Equipment	9
		2.3.4 Monitoring Methodology	9
	2.4	Landscape and Visual	10
		2.4.1 Monitoring Program	10
3	Mo	nitoring Results	11
	3.1	Impact Monitoring	11
	3.2	Air Quality Monitoring	11
		3.2.1 1-hour TSP	11
		3.2.2 24-hour TSP	11
	3.3	Noise Monitoring	12
	3.4	Landscape and Visual Impact	12
4	En	vironmental Site Inspection	13
	4.1	Site Inspection	13
		4.1.1 M+ Museum	13
		4.1.2 Lyric Theatre Complex	14
	4.2	Advice on the Solid and Liquid Waste Management Status	14
		4.2.1 M+ Museum	14
		4.2.2 Lyric Theatre Complex	14
	4.3	Status of Environmental Licenses and Permits	15
		4.3.1 M+ Museum	15

	4.4	 4.3.2 Lyric Theatre Complex Recommended Mitigation Measures 4.4.1 M+ Museum 4.4.2 Lyric Theatre Complex 	15 15 16 16
5	Cor	mpliance with Environmental Permit	17
6		cort in Non-compliance, Complaints, Notification of Summons and	18
	6.1	Record on Non-compliance of Action and Limit Levels	18
	6.2	Record on Environmental Complaints Received	18
	6.3	Record on Notifications of Summons and Successful Prosecution	18
7	Fut	ure Key Issues	19
	7.1	Construction Works for the Coming Month(s)	19
		7.1.1 M+ Museum	19
		7.1.2 Lyric Theatre Complex	19
	7.2	Key Issues for the Coming Month	20
		7.2.1 M+ Museum	20
		7.2.2 Lyric Theatre Complex	20
	7.3	Monitoring Schedule for the Coming Month	20
8	Cor	nclusions and Recommendations	21
	8.1	Conclusions	21
	8.2	Recommendations	21

Figure 1 Site Layout Plan and Monitoring Stations

Appendices

- A. Project Organisation
- B. Tentative Construction Programme
- C. Action and Limit Levels for Construction Phase
- D. Event and Action Plan for Air Quality, Noise, Landscape and Visual Impact
- E. Monitoring Schedule
- F. Calibration Certifications
- G. Graphical Plots of the Monitoring Results

- H. Meteorological Data Extracted from Hong Kong Observatory
- I. Waste Flow table
- J. Environmental Mitigation Measures Implementation Status
- K. Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Executive Summary

Mott MacDonald Hong Kong Limited (MMHK) was commissioned to undertake the Environmental Team (ET) services (including environmental monitoring and audit (EM&A)) for the construction of M+ Museum Main Works (Contract No.: CC/2015/3A/022) and Lyric Theatre Complex including the Foundation Works (Contract No.: CC/2015/3A/014) and L1 Contract (Contract No. CC/2017/3A/030) at West Kowloon Cultural District (WKCD) (The Project) as part of the WKCD development. The Project Proponent is the West Kowloon Cultural District Authority (WKCDA). The construction works and EM&A programme for M+ Museum and Lyric Theatre Complex commenced on 31 October 2015 and 1 March 2016 respectively.

The overall works for the WKCD fall under two separate categories of Designated Project (DP) of the Environmental Impact Assessment Ordinance (EIAO), namely an "engineering feasibility study of urban development projects with a study area covering more than 20 ha or involving a total population of more than 100 000" (Item 3 of Schedule 3) and "an underpass more than 100m in length under the built areas" (Item A.9, Part I, Schedule 2). An Environmental Permit No. EP-453/2013/B (EP) was issued with respect to the "Underpass Road and Austin Road Flyover Serving the West Kowloon Cultural District" which specifically includes the abovementioned category of DP under Item A.9, Part I, Schedule 2 of the EIAO.

This Monthly EM&A Report presents the monitoring works at M+ Museum and Lyric Theatre Complex from 1 April to 30 April 2019.

Exceedance of Action and Limit Levels

There was no breach of Action or Limit levels for Air Quality (1-hour TSP and 24-hour TSP) and Noise in this reporting month.

Implementation of Mitigation Measures

Construction phase weekly site inspections were carried out on 2, 9, 16, 23 and 30 April 2019 for M+ Museum and 3, 10, 17 and 24 April 2019 for Lyric Theatre Complex to confirm the implementation measures undertaken by the Contractors in the reporting month. The outcomes are presented in Section 4 and the status of implementation of mitigation measures in the site is shown in **Appendix J**.

Landscape and visual impact inspections were conducted as part of the abovementioned weekly site inspections during the reporting month. No adverse comment on landscape and visual aspects was made during these inspections.

Record of Complaints

No environmental complaint was recorded in the reporting month.

Record of Notification of Summons and Successful Prosecutions

No notification of summons and successful prosecution were recorded in the reporting month.

Future Key Issues

The major site works for M+ Museum scheduled to be commissioned in the coming month include:

- Structure
 - M+ Podium : Structural works completed
 - CSF RT/F: Structural works completed

- RDE 12-13F: Structure work for Slab rebar & column preparation
- Facade
 - Installation of panels on M+ tower up to RT/F
 - Erection of 1MF scaffold for 1MF Installation
 - Installation of façade on 2/F of RDE
- MEP
 - BEL, ELV, BFS, BPD, BME works from B2 to 3/F of M+
 - BEL, ELV, BFS, BPD, BME works from G/F to 15/F of RDE
 - BEL, ELV, BFS, BPD, BME works from G/F to 11/F
- ABWF
 - Block wall erection, Floor screed for plant room area and corridor area, wall plastering work up to M+ G/F
 - Blockwork plaster, paint/sealer, plaster, drywall subframe, Front of house work wall plastering work up to M+ 16/F
 - Steel platform, Plastering, Artwall/drywall stud erection, False ceiling sub-frame installation of RDE from 1MF to 2/F
 - Fairface remedial work, gypsum block, waterproofing, flor screed, foam glass and gypsum block, skim coat and painting, self-levelling screed, floating floor of CSF building from 1/F to 8/F

The major site works for Lyric Theatre Complex scheduled to be commissioned in the coming month include:

- Excavation and ELS works at Main Cofferdam
- Drainage and water mains work (PIW works)
- Extended basement structure construction of Area 06
- Artist Square (ASB) bored pile work near Area 6

Potential environmental impacts due to the construction activities, including air quality, noise, water quality, waste, landscape and visual, will be monitored or reviewed. The recommended environmental mitigation measures shall be implemented on site and regular inspections as required will be carried out to ensure that the environmental conditions are acceptable.

1 Introduction

1.1 Background

Mott MacDonald Hong Kong Limited (MMHK) was commissioned to undertake the Environmental Team (ET) services (including environmental monitoring and audit (EM&A)) for the construction of M+ Museum Main Works (Contract No.: CC/2015/3A/022) and Lyric Theatre Complex including the Foundation Works (Contract No.: CC/2015/3A/014) and L1 Contract (Contract No. CC/2017/3A/030) at West Kowloon Cultural District (WKCD) (The Project) as part of the WKCD development. The Project Proponent is the West Kowloon Cultural District Authority (WKCDA). The construction works and EM&A programme for M+ Museum and Lyric Theatre Complex commenced on 31 October 2015 and 1 March 2016 respectively.

The overall works for the WKCD fall under two separate categories of Designated Project (DP) of the Environmental Impact Assessment Ordinance (EIAO), namely an "engineering feasibility study of urban development projects with a study area covering more than 20 ha or involving a total population of more than 100 000" (Item 3 of Schedule 3) and "an underpass more than 100m in length under the built areas" (Item A.9, Part I, Schedule 2). An Environmental Permit No. EP-453/2013/B (EP) was issued with respect to the "Underpass Road and Austin Road Flyover Serving the West Kowloon Cultural District" which specifically includes the abovementioned category of DP under Item A.9, Part I, Schedule 2 of the EIAO. The captioned projects include part of the abovementioned underpass road located within the site boundary also falls under this same category.

The M+ museum development aims to provide an iconic presence for the M+ museum, semitransparent vertical plane, housing education facilities, a public restaurant and museum offices. At ground and lower levels, generous access will be provided to the park and other West Kowloon Cultural District facilities, alongside a public resource centre, theatres, retail and dining, and back-of-house functions.

The 1,200-seat Lyric Theatre Complex will be Hong Kong's first world-class facility for dance performances, including ballet, contemporary and Chinese dance forms. In the run up to the opening of further major performing arts venues in the WKCD, it will also be used for a wide variety of performing arts events including drama, opera and musical performances. The Lyric Theatre Complex will act as a platform for Hong Kong's leading arts organisations, and be a new major venue to show programmes from Asia and worldwide.

The Monthly EM&A Report is prepared in accordance with the Condition 3.4 of the Environmental Permit No. EP-453/2013/B. This Monthly EM&A Report presents the monitoring works at M+ Museum and Lyric Theatre Complex from 1 April to 30 April 2019. The purpose of this report is to summarise the findings in the EM&A of the project over the reporting period.

1.2 **Project Organisation**

The organisation chart and lines of communication with respect to the on-site environmental management structure together with the contact information of the key personnel are shown in **Appendix A**.

1.3 Environmental Status in the Reporting Period

During the reporting period, construction works at M+ Museum undertaken include:

- Structure
 - M+ Podium 1/F: Structural works

- CSF RT/F: Scaffold & formwork dismantling
- RDE 12-13F: Structure work for Slab rebar & column preparation
- Facade
 - Installation of panels on M+ tower up to 16/F
 - Erection of 1MF scaffold for 1MF Installation
 - Installation of façade on 2/F of RDE
- MEP
 - Cast-in items as per concrete pouring schedule
 - Fix work at M+ podium, RDE and CSF
- ABWF
 - RDE material delivery and block work up to 5/F
 - M+ material delivery and block work up to 11/F
 - CSF material delivery and block work up to 3-5/F

During the reporting period, construction works at Lyric Theatre Complex undertaken include:

4

- Excavation and ELS works at Main Cofferdam
- Drainage and water mains work (PIW works)
- Extended basement structure construction of Area 06
- Artist Square (ASB) bored pile work near Area 6

The Construction Works Programme of M+ Museum and Lyric Theatre Complex is provided in **Appendix B**. A layout plan of the Project is provided in **Figure 1**. Please refer to **Table 4.3** and **Table 4.4** on the status of the environmental licenses.

1.4 Summary of EM&A Requirements

The EM&A programme requires environmental monitoring of air quality, noise, landscape and visual as specified in the approved EM&A Manual.

A summary of impact EM&A requirements is presented in Table 1.1.

Parameters	Descriptions	Locations	Frequencies
Air Quality	24-Hour TSP	AM1 - International Commerce Centre	At least once every 6 days
	1-Hour TSP	AM1 - International Commerce Centre	At least 3 times every 6 days
	24-Hour TSP	AM2B – Austin Road West opposite to The Harbourside Tower 1	At least once every 6 days
	1-Hour TSP	AM2B – Austin Road West opposite to The Harbourside Tower 1	At least 3 times every 6 days
Noise	Leq, 30 minutes	NM1A- Podium level of The Harbourside Tower 1	Weekly
Landscape & Visual	Monitor implementation of proposed mitigation measures during the construction stage	As described in Table 9.1 and 9.2 of the EM&A Manual	Bi-weekly

Table 1.1: Summary of Impact EM&A Requirements

Given that the Project covers only a small part of the whole WKCD area (i.e. M+ Museum, Lyric Theatre Complex and respective portions of underpass road), it was proposed that the EM&A programme for the Project should only require 1 noise monitoring station and 2 air quality monitoring stations located

closest to the Project area. Currently, the works under the captioned project are confined in the western part of the WKCD site. Therefore, only the monitoring stations AM1, AM2 and NM1 were set up. Other monitoring locations are too far away (i.e. AM3 to AM5 and NM2 to NM5) are not included in this EM&A programme until the construction of the corresponding area commences.

The Harbourside management office formally rejected our proposal of setting up air quality and noise monitoring equipment on its premises at the podium level of Tower 1 (AM2/NM1) on 10 November 2015. Alternative noise monitoring location was identified at The Arch (NM2), however The Arch management office formally rejected our proposal of setting up noise monitoring equipment on its premises on 23 November 2015. Nevertheless, suitable air quality monitoring location at AM2 was identified on the ground floor in front of The Harbourside Tower 1, which is at the same location as that of baseline monitoring for consistency. No management approval is required at the ground floor for conducting the air monitoring. However, the electricity supply at AM2 was suspended from 31 August 2016 and was no longer available. In order to have a more secure electricity supply, an alternative air monitoring location (AM2A) was identified at Austin Road West opposite to The Harbourside Tower 1, which is close to Lyric Theatre Complex site entrance. This alternative air monitoring location was approved by EPD on 28 September 2016. Due to works programme, the air monitoring location AM2A has been relocated to the alternative monitoring location AM2B at the 1st floor of Gammon's site office, which was approved by EPD on 21 February 2019. Meanwhile, the opportunity of setting up the air monitoring location at The Harbourside is being explored. Noise monitoring at G/F of Harbourside will not be representative. Approval from the management office of the International Commerce Centre has been granted on 29 February 2016 for conducting noise monitoring at the alternative noise monitoring location identified at the podium floor (NM1A) which is free from screening to the construction activities. Therefore, 2 air quality monitoring stations and 1 noise impact monitoring station were confirmed for the impact monitoring.

The Environmental Quality Performance Limits for air quality and noise are shown in Appendix C.

The Event and Action Plan for air quality, construction noise. landscape and visual are shown in **Appendix D**.

The EM&A programme followed the recommended mitigation measures in the EM&A Manual. The EM&A requirements as well as the summary of implementation status of the environmental mitigation measures are provided in **Appendix J**.

2 Impact Monitoring Methodology

2.1 Introduction

For air quality and noise, the monitoring methodology, including the monitoring locations, monitoring equipment used, monitoring parameters, and frequency and duration etc., for air quality and noise are detailed in this Section. The environmental monitoring schedules for the reporting period and the tentative monitoring Schedule for the coming month are provided in **Appendix E**.

For landscape and audit impact, the relevant EM&A monitoring requirements and details are also presented in this Section.

2.2 Air Quality

2.2.1 Monitoring Parameters, Frequency and Duration

Table 2.1 summarizes the monitoring parameters, frequency and duration of the TSP monitoring.

Table 2.1: Air Quality Monitoring Parameters, Frequency and	and Duration
---	--------------

Parameter	Frequency	Duration
24-hour TSP	At least once in every six-days	24 hours
1-hour TSP	At least 3 times every six-days	60 minutes

2.2.2 Monitoring Locations

Currently, the works under the captioned project are confined in the western part of the WKCD site. Therefore, only the monitoring stations AM1 and AM2B were set up at the proposed locations in accordance with updated EM&A Manual. Location of the monitoring station is given in **Table 2.2** and shown in **Figure 1**.

Table 2.2: Air Quality Monitoring Station

Monitoring Station	Location
AM1	International Commerce Centre (ICC)
AM2B	Austin Road West opposite to The Harbourside Tower 1

2.2.3 Monitoring Equipment

Continuous 24-hour TSP air quality monitoring was conducted using High Volume Sampler (HVS) (Model: TE-5170) located at the designated monitoring station. The HVS meets all the requirements stated in of the EM&A Manual. Portable direct reading dust meter was used to carry out the 1-hour TSP monitoring. **Table 2.3** summarizes the equipment used in the impact air quality monitoring. Copies of the calibration certificates for the HVS, calibration kit and portable dust meters are attached in **Appendix F**.

Equipment	Model	
24-hour TSP monitoring		
High Volume Sampler	TE-5170 (Serial No.: 0767 and 8919)	
Calibrator	TE-5025A (Orifice I.D.: 2454)	
1-hour TSP monitoring		
Portable direct reading dust meter	Sibata LD-5R (Serial No.: 841723 and 841724)	

^{363512 | 05/02 | 0 |} May 2019

Calibration of the HVS (five point calibration) using Calibration Kit was carried out every two months. The HVS calibration orifice will be calibrated annually. Calibration certificate of the TE-5025A Calibration Kit and the HVS are provided in **Appendix F**

The 1-hour TSP monitoring should be determined periodically (e.g. annually) by the HVS to check the validity and accuracy of the results measured by direct reading method.

2.2.4 Monitoring Methodology

24-hour TSP Monitoring

Installation

The HVS was installed at the site boundary. The following criteria were considered in the installation of the HVS.

- A horizontal platform with appropriate support to secure the sampler against gusty wind was provided.
- The distance between the HVS and any obstacles, such as buildings, was at least twice the height that the obstacle protrudes above the HVS.
- A minimum of 2 metres separation from walls, parapets and penthouse was required for rooftop sampler.
- A minimum of 2 metres separation from any supporting structure, measured horizontally was required.
- No furnace or incinerator flues or building vent were nearby.
- Airflow around the sampler was unrestricted.
- The sampler has been more than 20 metres from any drip line.
- Permission was obtained to set up the sampler and to obtain access to the monitoring station.
- A secured supply of electricity is needed to operate the sampler.

Preparation of Filter Papers

- Glass fibre filters were labelled and sufficient filters that were clean and without pinholes were selected.
- The filters used are specified to have a minimum collection efficiency of 99 percent for 0.3 μm (DOP) particles.
- All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than ±3 °C with relative humidity (RH) < 50% and was not variable by more than ±5 %. A convenient working RH was 40%. All preparation of filters was done by Hong Kong Laboratory Accreditation Scheme (HOKLAS) accredited laboratory.

Field Monitoring Procedures

- The power supply was checked to ensure the HVS works properly.
- The filter holder and the area surrounding the filter were cleaned.
- The filter holder was removed by loosening the four bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully.
- The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter.
- The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges.
- The shelter lid was closed and was secured with the aluminium strip.
- The HVS was warmed-up for about 5 minutes to establish run-temperature conditions.
- A new flow rate record sheet was set into the flow recorder.
- The flow rate of the HVS was checked and adjusted at around 1.3 m³/min. The range specified in the EM&A Manual was between 0.6-1.7 m³/min.

- The programmable timer was set for a sampling period of 24 hours, and the starting time, weather condition and the filter number were recorded.
- The initial elapsed time was recorded.
- At the end of sampling, the sampled filter was removed carefully and folded in half length so that only surfaces with collected particulate matter were in contact.
- It was then placed in a clean plastic envelope and sealed.
- All monitoring information was recorded on a standard data sheet.
- Filters were sent to a Hong Kong Laboratory Accreditation Scheme (HOKLAS) accredited laboratory for analysis.

Maintenance and Calibration

- The HVS and its accessories are maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
- HVSs were calibrated upon installation and thereafter at bi-monthly intervals. The calibration kits were calibrated annually.
- Calibration records for HVS and calibration kit are shown in Appendix F.

1-hour TSP Monitoring

Field Monitoring

The measuring procedures of the 1-hour dust meter are in accordance with the Manufacturer's Instruction Manual as follows:

- Turn the power on.
- Close the air collecting opening cover.
- Push the "TIME SETTING" switch to [BG].
- Push "START/STOP" switch to perform background measurement for 6 seconds.
- Turn the knob at SENSI ADJ position to insert the light scattering plate.
- Leave the equipment for 1 minute upon "SPAN CHECK" is indicated in the display.
- Push "START/STOP" switch to perform automatic sensitivity adjustment. This measurement takes 1 minute.
- Pull out the knob and return it to MEASURE position.
- Setting time period of 1 hour for the 1-hour TSP measurement.
- Push "START/STOP" to start the 1-hour TSP measurement.
- Regular checking of the time period setting to ensure monitoring time of 1 hour.

Maintenance and Calibration

- The 1-hour dust meter would be checked at 3-month intervals and calibrated at 1-year intervals throughout all stages of the air quality monitoring.
- Calibration records for direct dust meters are shown in Appendix F.

Weather Condition

 Meteorological data extracted from Hong Kong Observatory for the reporting month is provided in Appendix H.

2.3 Noise

2.3.1 Monitoring Parameters, Frequency and Duration

Table 2.4 summarizes the monitoring parameters, frequency and duration of noise monitoring. The noise in A-weighted levels L_{eq} , L_{10} and L_{90} are recorded in a 30-minute interval between 0700 and 1900 hours.

Table 2.4: Noise Monitoring Parameters, Period and Frequency

Time Period	Parameters	Frequency
Daytime on normal weekdays	L _{eq} (30 min), L ₉₀ (30 min) & L ₁₀ (30 min)	Once every week
(0700-1900 hours)		

2.3.2 Monitoring Location

Currently, the works under the captioned project are confined in the western part of the WKCD site. Therefore, only the monitoring station NM1A was set up at the proposed location in accordance with updated EM&A Manual. Location of the monitoring station is given in **Table 2.5** and shown in **Figure 1**.

Table 2.5: Noise Monitoring Station

Monitoring Station	Location
NM1A	Podium floor of International Commerce Centre (ICC)

2.3.3 Monitoring Equipment

Integrating Sound Level Meter was used for noise monitoring. It was a Type 1 sound level meter capable of giving a continuous readout of the noise level readings including equivalent continuous sound pressure level (L_{Aeq}) and percentile sound pressure level (L_x). They comply with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). **Table 2.6** summarizes the noise monitoring equipment model being used.

Table 2.6: Noise Monitoring Equipments

Monitoring Station	Equipment Model		
	Integrating Sound Level Meter	Calibrator	
NM1A	Rion NL-52 (Serial No. 00175561)	LARSON DAVIS CAL200 (Serial No. 15678)	

2.3.4 Monitoring Methodology

Field Monitoring

- The microphone of the Sound Level Meter was set at least 1.2 m above the ground.
- Free Field measurement was made at the monitoring locations.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - frequency weighting: A
 - time weighting: Fast
 - time measurement: 30 minutes intervals (between 0700-1900 on normal weekdays)
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1 kHz. If the difference in the calibration level before and after measurement was more than 1 dB, the measurement would be considered invalid and has to be repeated after recalibration or repair of the equipment.
- During the monitoring period, the L_{eq}, L₁₀ and L₉₀ were recorded. In addition, any site observations and noise sources were recorded on a standard record sheet.
- A correction of +3dB(A) was made to the free field measurements.

Maintenance and Calibration

- The microphone head of the sound level meter and calibrator is cleaned with soft cloth at quarterly intervals.
- The sound level meter and calibrator are sent to the supplier or HOKLAS laboratory to check and calibrate at yearly intervals.
- Calibration records are shown in **Appendix F**.

Weather Condition

 Meteorological data extracted from Hong Kong Observatory for the reporting month is provided in Appendix H.

2.4 Landscape and Visual

2.4.1 Monitoring Program

Table 2.7 details the monitoring program (as proposed in the WKCD EIA report) for landscape and visual impact during the construction phase.

Table 2.7:	Monitoring Program for Landscape and Visual Impact during Construction Phase

Stage	Monitoring Task	Frequency	Report	Approval
Construction	Monitor implementation of proposed mitigation measures during the construction stage.	,	ET to report Contractor's compliance	on Counter-signed by IEC

During the landscape and visual impact monitoring, any changes in relation to the landscape and visual amenity should be monitored with reference to the baseline conditions of the site. In addition, mitigation measures were proposed in the WKCD EIA report to minimise the landscape and visual impacts during the construction phase. The proposed mitigation measures as shown in Table 9.1 and Table 9.2 of the EM&A Manual should be checked for proper implementation.

3 Monitoring Results

3.1 Impact Monitoring

Construction impact monitoring for air quality, noise and landscape and visual impact was undertaken in compliance with the EM&A Manual during the reporting month.

3.2 Air Quality Monitoring

17-Apr-19

23-Apr-19

29-Apr-19

1-Apr-19

6-Apr-19

11-Apr-19

17-Apr-19

23-Apr-19

29-Apr-19

3.2.1 1-hour TSP

Results of 1-hour TSP at the monitoring location AM1 and AM2B are summarised in **Table 3.1**. Graphical plots of the monitoring results are shown in **Appendix G**.

38

38

39

47

68

97

52

54

49

32

44

33

44

69

94

50

55

52

44 - 97

274.2

Monitoring	Monitoring	Start	1-hour TSP (µg/m³)			Range	Action
Station	Date	Time	1st Result	2nd Result	3rd Result	_ (μg/m³)	Level (µg/m³)
	1-Apr-19	8:00	42	39	45		
	6-Apr-19	8:02	64	61	60	_	
	11-Apr-19	7:50	74	69	79	00 70	070 7
AM1						32 - 79	273.7

41

41

41

49

71

91

45

49

44

Table 3.1: Summary of 1-hour TSP monitoring results

7:52

7:53

7:52

8:17

8:16

8:07

8:07

8:07

8:07

3.2.2 24-hour TSP

AM2B

Results of 24-hour TSP at the monitoring location AM1 and AM2B are summarised in **Table 3.2**. Graphical plots of the monitoring results are shown in **Appendix G**.

I able 3.2:	3.2: Summary of 24-hour TSP monitoring results					
Monitoring Station	Monitoring Date	Start Time	Monitoring Results (μg/m3)	Range (µg/m3)	Action Level (µg/m3)	Limit Level (µg/m3)
	1-Apr-19	8:02	43			
	6-Apr-19	8:00	44	-		
AM1	11-Apr-19	7:52	63	- 27 - 63	142.6	260
	17-Apr-19	7:50	52	27 - 63	143.6	260
	23-Apr-19	10:20	39	-		
	29-Apr-19	7:50	27	-		
	1-Apr-19	8:15	64			
AM2B	6-Apr-19	8:14	56	47 - 80	151.1	260
	11-Apr-19	8:05	80	-		

Table 3.2: Summary of 24-hour TSP monitoring results

363512 | 05/02 | 0 | May 2019

Limit

Level

(µg/m³)

500

500

Monitoring Station	Monitoring Date	Start Time	Monitoring Results (μg/m3)	Range (µg/m3)	Action Level (µg/m3)	Limit Level (µg/m3)
	17-Apr-19	8:05	63			
	23-Apr-19	8:05	47	-		
	29-Apr-19	8:05	52			

No exceedance of 1-hour and 24-hour TSP (Action or Limit Level) was ecorded in the reporting period.

3.3 Noise Monitoring

The construction noise monitoring results at the monitoring location NM1A are summarized in **Table 3.3**. Graphical plots of the monitoring data and the station set-up of a free-field measurement are shown in **Appendix G**.

Monitoring Date	Start Time	End Time	Leq (30 mins)*, dB(A)	Limit Level for Leq (dB(A))			
1-Apr-19	10:24	10:54	69				
11-Apr-19	10:14	10:44	68	-			
17-Apr-19	10:14	10:44	69	75			
23-Apr-19	10:10	10:40	68	-			
29-Apr-19	10:12	10:42	69	-			

Table 3.3: Summary of noise monitoring results during normal weekdays

Remarks:

* +3dB (A) correction was applied to free-field measurement.

No exceedance (Action/Limit Level) of construction noise was recorded in the reporting period as no noise related environmental complaint was received during the reporting period and noise levels recorded during the monitoring period were below 75 dB(A).

3.4 Landscape and Visual Impact

Landscape and visual impact inspections were conducted as part of the weekly site inspections on 2, 16 and 30 April 2019 for M+ Museum, and 10 and 24 April 2019 for Lyric Theatre Complex during the reporting month. As reviewed by the registered Landscape Architect, no adverse comment on landscape and visual aspects was made during these inspections.

The landscape and visual mitigation measures were implemented during the reporting period. The summary of implementation status of the environmental mitigation measures is provided in **Appendix J**.

4 Environmental Site Inspection

4.1 Site Inspection

4.1.1 M+ Museum

Construction phase weekly site inspections were carried out on 2, 9, 16, 23 and 30 April 2019. The joint site inspection with IEC, ET, ER and Contractor was held on 16 April 2019. All observations have been recorded in the site inspection checklist and passed to the Contractor together with the appropriate recommended mitigation measures where necessary.

The key observations from the site inspections and associated recommendations are summarized in **Table 4.1**.

Inspection Date	Parameter	Observation / Recommendation	Contactor's Responses / Action(s) Undertaken	Close-out (Date)
2 Apr 2019	Air quality	Cement bags were found without proper cover. The contractor was reminded to cover them with impervious sheeting to reduce dust impact.	The contractor has covered the cement bags with impervious sheeting.	9 Apr 2019
2 Apr 2019	Water quality	Effluent quality was checked. It was found visually clear when comparing with standard solution and with proper pH range.	N/A	N/A
2 Apr 2019	Waste management	Chemicals were found without drip tray. The contractor was reminded to provide drip tray or remove them if not in use.	The contractor has removed the chemicals.	9 Apr 2019
9 Apr 2019	Water quality	Effluent quality was checked. It was found visually clear when comparing with standard solution and within proper pH range.	N/A	N/A
16 Apr 2019	Noise	The hand-held breaker was found without noise emission label. The contractor was reminded to provide noise emission label for the breaker.	The contractor has provided the noise emission label for the breaker.	18 Apr 2019
16 Apr 2019	Water quality	Effluent quality of wetsep was checked. It was found visually clear when comparing with standard solution and within proper pH range.	N/A	N/A
23 Apr 2019	Water quality	Effluent quality of wetsep was checked. It was found visually clear when comparing with standard solution and within proper pH range.	N/A	N/A
30 Apr 2019	Water quality	High pH value (9.73) which outside the acceptable range (i.e. pH 6 to 9) was observed at wetsep. The Contractor was reminded to rectify the problem before discharging the effluent offsite.	Follow-up status will be provided in the next reporting month.	On-going

Table 4.1: Summary of Site Inspections and Recommendations for M+ Museum

4.1.2 Lyric Theatre Complex

Construction phase weekly site inspections were carried out on 3, 10, 17 and 24 April 2019. The joint site inspection with IEC, ET, ER and Contractor was held on 24 April 2019. All observations have been recorded in the site inspection checklist and passed to the Contractor together with the appropriate recommended mitigation measures where necessary.

The key observations from the site inspections and associated recommendations are summarized in **Table 4.2**.

Inspection Date	Parameter	Observation / Recommendation	Contactor's Responses / Action(s) Undertaken	Close-out (Date)
27 Mar 2019	Water Quality	The contractor has been reminded to remove the sediment in the wetseps to ensure proper operation.	The contractor had removed the sediment in the wetseps.	3 Apr 2019
27 Mar 2019	Air Quality	The contractor has been reminded to provide wheel washing in stockpile area before leaving site.	The contractor had provided wheel washing in stockpile area before leaving site	3 Apr 2019
3 Apr 2019	Water Quality	The contractor had been reminded to remove the sediment in wetsep #1 and #3 to ensure proper operation.	The contractor had removed the sediment in wetsep #1 and #3 to ensure proper operation.	9 Apr 2019
3 Apr 2019	Waste Management	The contractor had been remined to provide drip tray for chemicals.	The contractor had provided drip tray for chemicals	9 Apr 2019
10 Apr 2019	Water Quality	Turbid water was observed on wetsep. Contractor had been reminded to clear the turbid to keep good quality of discharge water.	The contractor had cleared the turbid to keep good quality of discharge water.	12 Apr 2019
24 Apr 2019	Water Quality	Turbid water was observed at wetsep. The contractor was reminded to clear the suspended solid in order to keep the quality of discharge effluent.	Follow-up status will be provided in the next reporting month.	On-going

Table 4.2: Summary of Site Inspections and Recommendations for Lyric Theatre Complex

4.2 Advice on the Solid and Liquid Waste Management Status

The Contractors have been registered as a chemical waste producer for the Project. Construction and demolition (C&D) material sorting will be carried out on site. A sufficient number of receptacles were available for general refuse collection.

4.2.1 M+ Museum

As advised by the Contractor, 127.3 tonnes of inert C&D material were disposed of as public fill to Tseung Kwan O Area 137, while 477.4 tonnes of general refuse were disposed of at SENT landfill. 0 tonne of metals, 0 tonne of paper/cardboard packaging, 0 tonne of plastic and 300.0 tonnes of timber were collected by recycling contractors in the reporting month. 0 tonne of inert C&D materials was reused on site. 0 tonne of inert C&D materials were reused in other projects and 200.2 tonnes of inert C&D materials were disposed to sorting facility. 0.9 tonne of chemical waste was collected by licensed contractors in the reporting period.

The cumulative waste generation records for M+ Museum are shown in Appendix I.

4.2.2 Lyric Theatre Complex

As advised by the Contractor, 5,835.39 tonnes and 1,444.18 tonnes of inert C&D material were disposed of as public fill to Tseung Kwan O Area 137 and Tuen Mun Area 38 Public Fill, while 24.9 tonnes of general refuse were disposed of at SENT and WENT landfill. 32.6 tonnes of metals, 0 tonne of paper/cardboard packaging, 0.8 tonne of plastic and 0 tonne of timber were collected by recycling

contractors in the reporting month. 0 tonne of inert C&D materials was reused on site. 21394.3 tonnes of inert C&D materials were reused in other projects and 0 tonnes of inert C&D materials were imported for reuse at site. 0 tonne of chemical waste were collected by licensed contractors in the reporting period.

The actual amounts of different types of waste generated by the activities of construction works at Lyric Theatre Complex in the reporting month are shown in **Appendix I**.

4.3 Status of Environmental Licenses and Permits

The environmental permits, licenses, and/or notifications on environmental protection for this Project which were valid during the period are summarised in **Tables 4.3** and **4.4**.

4.3.1 M+ Museum

Table 4.3: Status of Environmental Submissions, Licenses and Permits for M+ Museum

Permit / License	Valid	Period	Status	Remarks
No. / Notification / Reference No.	From	То	_	
Chemical Waste Produ	cer Registration			
5213-217-G2347-53	04-Oct-18		Valid	
Billing Account Constr	uction Waste Dispos	al		
7031993	03-Oct-18		Account Active	
Construction Noise Per	rmit			
GW-RE0094-19	16-Feb-19	03-Aug-19	Valid	
Wastewater Discharge	License			
WT-00033363-2019	21-Mar-19	31-Mar-24	Valid	
Notification under Air F	Pollution Control (Co	nstruction Dust) Regu	Ilation	
437339	12-Sep-18		Notified	

4.3.2 Lyric Theatre Complex

Table 4.4:Status of Environmental Submissions, Licenses and Permits for Lyric TheatreComplex

Permit / License	Valid	Period	Status	Remarks
No. / Notification / Reference No.	From	То		
Chemical Waste Produc	cer Registration			
5213-217-G2347-39	17-Feb-16		Valid	
Billing Account Constru	uction Waste Dispos	al		
7029925	22-Jan-18		Account Active	
Construction Noise Per	rmit			
GW-RE0862-18	18-Dec-18	16-Jun-19	Valid	
Wastewater Discharge	License			
WT-00030694-2018	6-Apr-18	30-Apr-23	Valid	
Notification under Air P	Pollution Control (Co	nstruction Dust) Regu	ılation	
429708	16-Jan-18		Notified	

4.4 Recommended Mitigation Measures

The EM&A programme followed the recommended mitigation measures in the EM&A Manual. The EM&A requirements as well as the summary of implementation status of the environmental mitigation

363512 | 05/02 | 0 | May 2019 \\mottmac\Project\Hong Kong\ENL\PROJECTS\363512 WKCD M+ Superstructure\05 Deliverables\02 Monthly EM&A Report\(42) Monthly EM&A Report for Apr 2019\Rev.0\Monthly EM&A Report for Apr 2019_v0.docx measures are provided in **Appendix J**. In particular, the following mitigation measures were brought to attention during the site inspections:

4.4.1 M+ Museum

Air Quality

- Cement bags should be covered entirely by impervious sheeting to reduce dust impact.

Waste Management

- Drip trays should be provided for all chemicals on site.

Noise

Noise emission labels should be provided for hand-held breakers having a mass of above 10 kg.

Water Quality

 All drainage facilities should be regularly maintained to ensure proper and efficient operation at all times.

4.4.2 Lyric Theatre Complex

Water Quality

 All drainage facilities should be regularly maintained to ensure proper and efficient operation at all times.

Waste Management

- Drip trays should be provided for all chemicals on site.

5 Compliance with Environmental Permit

The status of the required submission under the EP during the reporting period is summarized in **Table 5.1**.

Table 5.1: Status of Submissions under the Environmental Permit

EP Condition	Submission	Submission Date
Condition 3.4	Monthly EM&A Report for March 2019	12 April 2019

6 Report in Non-compliance, Complaints, Notification of Summons and Successful Prosecutions

6.1 Record on Non-compliance of Action and Limit Levels

There was no breach of Action or Limit Levels for Air Quality and Noise monitoring in the reporting month.

6.2 Record on Environmental Complaints Received

No environmental complaint was received in the reporting month. The cumulative statistics on complaints were provided in **Appendix K**.

6.3 Record on Notifications of Summons and Successful Prosecution

No notifications of summons or successful prosecution were received this month. The cumulative statistics on notifications of summons and successful prosecutions were provided in **Appendix K**.

7 Future Key Issues

7.1 Construction Works for the Coming Month(s)

7.1.1 M+ Museum

The major site works for M+ Museum scheduled to be commissioned in the coming month include:

- Structure
 - M+ Podium : Structural works completed
 - CSF RT/F: Structural works completed
 - RDE 12-13F: Structure work for Slab rebar & column preparation
- Facade
 - Installation of panels on M+ tower up to RT/F
 - Erection of 1MF scaffold for 1MF Installation
 - Installation of façade on 2/F of RDE
- MEP
 - BEL, ELV, BFS, BPD, BME works from B2 to 3/F of M+
 - BEL, ELV, BFS, BPD, BME works from G/F to 15/F of RDE
 - BEL, ELV, BFS, BPD, BME works from G/F to 11/F
- ABWF
 - Block wall erection, Floor screed for plant room area and corridor area, wall plastering work up to M+ G/F
 - Blockwork plaster, paint/sealer, plaster, drywall subframe, Front of house work wall plastering work up to M+ 16/F
 - Steel platform, Plastering, Artwall/drywall stud erection, False ceiling sub-frame installation of RDE from 1MF to 2/F
 - Fairface remedial work, gypsum block, waterproofing, flor screed, foam glass and gypsum block, skim coat and painting, self-levelling screed, floating floor of CSF building from 1/F to 8/F

7.1.2 Lyric Theatre Complex

The major site works for Lyric Theatre Complex scheduled to be commissioned in the coming month include:

- Excavation and ELS works at Main Cofferdam
- Drainage and water mains work (PIW works)
- Extended basement structure construction of Area 06
- Artist Square (ASB) bored pile work near Area 6

Excavation and ELS works at Main Cofferdam, drainage and water mains work (PIW works), extended basement structure construction of Area 06 and Artist Square (ASB) bored pile work near Area 6. 19

7.2 Key Issues for the Coming Month

7.2.1 M+ Museum

Key issues to be considered in the coming month include:

- Generation of dust from construction works;
- Noise impact from operating equipment and machinery on-site;
- Generation of site surface runoffs and wastewater from activities on-site;
- Management of stockpiles and slopes, particularly on rainy days;
- Sorting, recycling, storage and disposal of general refuse and construction waste; and
- Management of chemicals and avoidance of oil spillage on-site.

7.2.2 Lyric Theatre Complex

Key issues to be considered in the coming month include:

- Generation of dust from construction works;
- Noise impact from operating equipment and machinery on-site;
- Generation of site surface runoffs and wastewater from activities on-site;
- Management of stockpiles and slopes, particularly on rainy days;
- Sorting, recycling, storage and disposal of general refuse and construction waste; and
- Management of chemicals and avoidance of oil spillage on-site.

7.3 Monitoring Schedule for the Coming Month

The environmental site inspection and environmental monitoring will be continued in the coming month. Impact monitoring for air quality and noise in accordance with the approved EM&A Manual has commenced since 31 October 2015 and 5 March 2016 respectively. The tentative monitoring schedule for the coming month is shown in the **Appendix E**.

8 Conclusions and Recommendations

8.1 Conclusions

The EM&A programme as recommended in the EM&A Manual has been undertaken since the construction of M+ Museum main works commenced on 31 October 2015, and the construction of Lyric Theatre Complex commenced on 1 March 2016.

Monitoring of air quality and noise with respect to the Projects is underway. In particular, the 1-hour TSP, 24-hour TSP, noise level (as Leq, 30 minutes) under monitoring have been checked against established Action and Limit levels. There was no breach of Action and Limit Levels for 1-hour TSP, 24-hour TSP and noise in the reporting month.


No environmental complaint, notifications of summons or successful prosecution were received during the reporting month.

Weekly construction phase site inspections and bi-weekly landscape and visual impact inspections were conducted during the reporting month as required. It was observed that the Contractors had implemented all possible and feasible mitigation measures to mitigate the potential environmental impacts during construction phase works.

8.2 Recommendations

Potential environmental impacts due to the construction activities, including air quality, noise, water quality, waste, landscape and visual, will be monitored or reviewed. The recommended environmental mitigation measures shall be implemented on site and regular inspections as required will be carried out to ensure that the environmental conditions are acceptable.

Figure 1 Site Layout Plan and Monitoring Stations

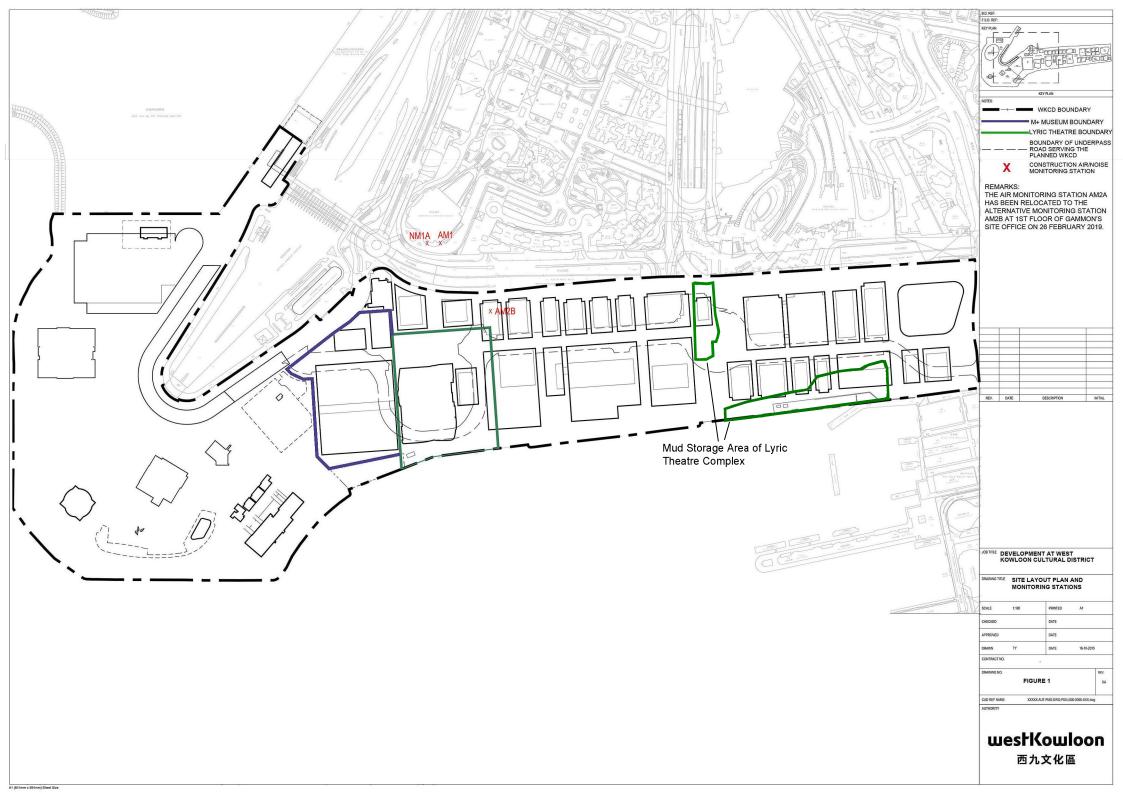

Appendices

- A. Project Organisation
- B. Tentative Construction Programme
- C. Action and Limit Levels for Construction Phase
- D. Event and Action Plan for Air Quality, Noise, Landscape and Visual Impact
- E. Monitoring Schedule
- F. Calibration Certifications
- G. Graphical Plots of the Monitoring Results
- H. Meteorological Data Extracted from Hong Kong Observatory
- I. Waste Flow table
- J. Environmental Mitigation Measures Implementation Status
- K. Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

A. Project Organisation

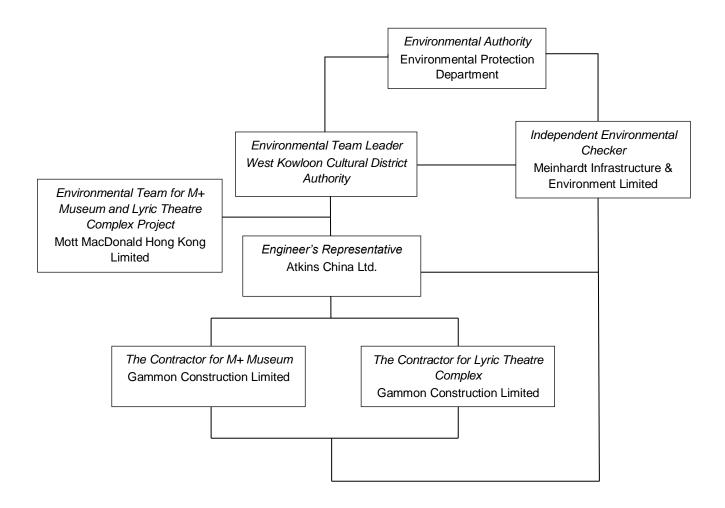


Table A-1: Contact information

Company Name	Role	Name	Telephone
Atkins China Ltd.	Assistant Resident Engineer	Ms. Gloria Lui	5506 6361
Meinhardt Infrastructure & Environment Limited	Independent Environmental Checker	Mr. Fredrick Leong	2859 1739
Gammon Construction Limited (M+ Museum)	Environmental Manager	Mr. Andy Leung	9489 0035
Gammon Construction Limited (Lyric Theatre Complex)	Environmental Manager	Ms. Sammie Chan	9864 4296
Mott MacDonald Hong Kong Ltd.	Contractor's Environmental Team Leader	Mr. Thomas Chan	2828 5757
West Kowloon Cultural District Authority	Senior Environmental Specialist	Mr. Brian Tam	2200 0059

B. Tentative Construction Programme

25

M+ Museum

		-	-	-		arget Program (Re	v_0; 28Jan19) -	CMWP_R0								age 1	/ 4
ID	Activity	OD	Start	Finish	TF	Qtr 4 p Oct Nov Dec	Qtr 1 Jan Feb Mar	Qtr 2 Apr May		Qtr 3	Sep	Qtr 4 Oct Nov Dec	Qtr 1 Jan Feb		Qtr 2		tr 3 Jul
	+ Project Remaining Works @ 10 Sep 2018 Target Program (Rev_0; 28Jan1 AL & PRELIMINARIES (Remaining Works @ 10 SEP 2018)	9)	•								+ • • • •			·····			
PROJE	CT KEY COMPLETION DATES									· · · · · · · · · · · · · · · · · · ·							
OP1	tion Obligations (*constrained dates for critical paths) Podium, M+ Tower & CSF - Obtain OP for the Whole of M+	0		31-Mar-20*	0												
PC2 OP2	CSF - Obtain PC for H'over to Employer (Incl. Zone B2_Z07 - Loading Bays) RDE - Obtain OP for H'over to Employer	0		31-Mar-20* 30-May-20*	1 1												
PC1 BASEME	Podium, M+ Tower & RDE - Obtain PC for Hover to Employer ENT & PODIUM	0		30-Jun-20*	0				-	·	++		·				
Constru										 							
	rium > GF ? Summary										++						
1202	[LoE] POD_GF_AUD - Rem Structural Works	140	29-Dec-18	21-Jun-19	180					·	++						
9350 9351	[LoE] POD_GF_AUD - MEP 1st, 2nd & final fix [LoE] POD_GF_AUD - ABWF Works	165 253	23-Apr-19 23-Apr-19	07-Nov-19 28-Feb-20	5 101						· · · · · · · · ·						
	s (B1-GF) 2 Summary				_						++						
9352 9361	[LoE] POD_GF_Cinema - Structural Works	120 116	11-Feb-19 18-Jul-19	04-Jul-19 03-Dec-19	2 13			*****	*****			· · · · · · · · · · · · · · · · · · ·					
9371	[LoE] POD_GF_Cinema - MEP Works [LoE] POD_GF_Cinema - ABWF Works	139	02-Jul-19	13-Dec-19	52					KXXXXXX	******						
	Image Centre Lobby/Bar & Museum Shop No.2 (B1-GF) - POD_B1_Z09b 2 Summary									·							
9380 9381	LoE] POD_B1_Z09b - Struct'l Works LoE] POD_B1_Z09b - MEP Works	97 83	09-Apr-19 26-Aug-19	02-Aug-19 03-Dec-19	17							······					
9382 9489	LoE] POD_B1_Z09b - ABWF Wrks (Drying w/ Wild Air not req'd) LoE] POD_B1_Z09b - ABWF Wrks (Drying w/ Wild Air req'd)	100 41	26-Jul-19 27-Nov-19	22-Nov-19 15-Jan-20	1 132												
Lecture	Theatre & Adja cent Areas	41	27-1107-13	13-5411-20	132					· · · · · · · · · · · · · · · · · · ·		·····					
1203	2 Summary [LoE] POD GF LTH - Struct'I WOrks	203	15-Nov-18	23-Jul-19	10			· · · · · · · · · · · · · · · · · · ·		××							
8205 8204	[LoE] POD_GF_LTH - MEP Works [LoE] POD_GF_LTH - ABWF Wiks (Drying w/ Wild Air not req'd)	95 166	03-Jul-19 03-Jun-19	24-Oct-19 18-Dec-19	35 148					· · · · · · · · · · · · · · · · · · ·	÷÷						
9383	[LoE] POD_GF_LTH - ABWF Wiks (Drying w/ Wild Air req'd)	45	18-Nov-19	10-Jan-20	136					·	$\frac{1}{1}$ $\frac{1}{1}$						
	g Centre & Adjacent Areas (GF & 1/F) 2 <i>Summary</i>										+ + + + + + + + + + + + + + + + + + +						
9398 9399	[LoE] POD_GF_LC & Adj Areas (GF & 1/F) - Struct'l Wrks [LoE] POD_GF_LC & Adj Areas (GF & 1/F) - MEP Wrks	160 129	24-Sep-18 29-May-19	11-Apr-19 31-Oct-19	71 89				-¦ -	· · · · · · · · · · · · · · · · · · ·	+ + + +				- <mark> </mark>		
9426	[LoE] POD_GF_LC & Adj Areas (GF & 1/F) - ABWF Wrks (Drying w/ Wild Air not req	140	18-May-19	02-Nov-19	193					·	++						
9451 Moving	[LoE] POD_GF_LC & Adj Areas (GF & 1/F)_L2SUM - ABWF Wrks (Drying w/ Wild A Image Centre (GF-1M) - POD_GF_Z01	42	18-Nov-19	07-Jan-20	139					·							
Level 2 9452	2 Summary [LoE] POD_GF_Z01_MIC (GF-1M) - Struct'l Works	111	28-Sep-18	15-Feb-19	51					· · · · · · · · · · · · · · · · · · ·							
9453	[LoE] POD_GF_Z01_MIC (GF-1M - MEP Works	101	22-May-19	19-Sep-19	63			C		· · · · · · · · · · · · · · · · · · ·	÷	·····					
9454 Found 8	[LoE] POD_GF_Z01_MIC (GF-1M - ABWF Works Industrial Spaces (B2-GF) - POD_B2_Z13	163	23-Apr-19	05-Nov-19	191					·	++						
Level 2 9852	2 Summary [LoE] POD_GF_B2_Z13_Fnd & Ind'I Sps (B2-GF) - Struct Works _Floating Slab	60	23-May-19	02-Aug-19	50					· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·					
9455	[LoE] POD_GF_B2_Z13_Fnd & Ind'I Sps (B2-GF) - MEP Wrks	90	04-Jul-19	19-Oct-19	16			· · · · · · · · · · · · · · · · · · ·		 	++						
9456 9457	[LoE] POD_GF_B2_Z13_Fnd & Ind'I Sps (B2-GF) - ABWF Wrks (Drying w/ Wild Air [LoE] POD_GF_B2_Z13_Fnd & Ind'I Sps (B2-GF) - ABWF Wrks (Drying w/ Wild Air	164 82	09-May-19 20-Nov-19	21-Nov-19 04-Mar-20	99 97												
Level 8	2 2 Summary													· · · · · · · · · · · · · · · · · · ·			
9458	[LoE] POD_B2 - Struct'l Works	192	26-Nov-18	20-Jul-19	37		++	+			++						
9459 9460	[LoE] POD_B2_Z01 to B2_Z04_Plant Rms - MEP Works [LoE] POD_B2_Z01 to B2_Z04_Plant Rms - ABWF Works	282 279	12-Oct-18 03-Dec-18	21-Sep-19 09-Nov-19	61 187				-! !		·····						
9461 9462	[LoE] POD_B2_Z05 to B2_Z06_Toilets - MEP Works [LoE] POD_B2_Z05 to B2_Z06_Toilets - ABWF Wrks (Drying w/ Wild Air not req'd)	127 142	13-Apr-19 28-Mar-19	11-Sep-19 13-Sep-19	129 227				-; ;								
9767 9465	[LoE] POD_B2_Z05 to B2_Z06_Toilets - ABWF Wrks (Drying w/ Wild Air req'd) [LoE] POD_B2_Z07 to B2_Z08_Plant Rms - MEP Works	18 223	18-Nov-19 26-Feb-19	07-Dec-19 20-Nov-19	163 12			~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~	~~~~~	*****	×××××						
9466	[LoE] POD_B2_Z07 to B2_Z08_Plant Rms - ABWF Works	354	17-Dec-18	29-Feb-20	100						1 1	·					
	2 Summary									· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·			· · · · · · · · · · · · · · · · · · ·			
9471 9472	[LoE] POD_B1 - Structural Works [LoE] POD_B1_Z02 to B1_Z05_ BoH/Plant Rm/Kit - MEP Works	213 247	27-Oct-18 22-Jan-19	16-Jul-19 20-Nov-19	26 160						<u>+</u> +						
9475 9476	[LoE] POD_B1_Z02 to B1_Z05_BoH/Plant Rm/Kit - ABWF Works [LoE] POD_B1_Z06_Toilets - MEP Works	274 244	09-Jan-19 26-Feb-19	09-Dec-19 14-Dec-19	162 51												
9477 9479	[LoE] POD_B1_Z06_Toilets - ABWF Works [LoE] POD_B1_Z07_BoH/Lobbies/Non-FR Corr - MEP Works	293 156	02-Jan-19 26-Feb-19	24-Dec-19 30-Aug-19	149 79						<u>+</u> +	·					
9480	[LoE] POD_B1_Z07_BoH/Lobbies/Non-FR Corr - ABWF Works	211	11-Feb-19	22-Oct-19	203						-						
9482 9483	[LoE] POD_B1_Z08/09a/10_FoH MEP Works [LoE] POD_B1_Z08/09a/10_FoH ABWF Works	137 233	24-Jun-19 17-Jun-19	04-Dec-19 28-Mar-20	0 76						·····						
9484 9485	[LoE] POD_B1_Z11/12/14/16/17/18a_BoH/R Corr/Lobby/Carpark_Z - MEP Works [LoE] POD_B1_Z11/12/14/16/17/18a_BoH/R Corr/Lobby/Carpark ABWF Works	215 246	26-Feb-19 04-Mar-19	11-Nov-19 23-Dec-19	20 150									· · · · · · · · · · · · · · · · · · ·			
9486 9487	[LoE] POD_B1_Z15_Carriageway & Ramp - Stage 1_ABWF & MEP Works [LoE] POD_B1_Z15_Carriageway & Ramp - Stage 2_ABWF & MEP Works	90 78	23-Apr-19 27-Aug-19	08-Aug-19 28-Nov-19	74 97						1 1			 			
Level Lo										·	++		·				
9488	2 Summary [LoE] POD_LG - Structural Works	58	15-May-19	23-Jul-19	1				·	<u>∞∞</u>	· · · · · · · · · · · · · · · · · · ·						
9490 9491	[LoE] POD_LG_Z01/02/03_BoH/FR Corr/Lob/Carpark - MEP Works [LoE] POD_LG_Z01/02/03_BoH/FR Corr/Lob/Carpark - ABWF Works	144 227	26-Feb-19 28-Jan-19	16-Aug-19 02-Nov-19	91 193				-!!								
9492 9493	[LoE] POD_LG_Z04/5/6/18d_Multi-Media/Cine Lob/Corr/BoH - MEP Works [LoE] POD_LG_Z04/5/6/18d_Multi-Media/Cine Lob/Corr/BoH - ABWF Works	113 163	22-Jul-19 10-Jul-19	03-Dec-19 21-Jan-20	1 127			, , , , , , , , , , , , , , , , , , ,			÷*****						
Level G	F										· + + + + + + + + + + + + + +			· · · · · · · · · · · · · · · · · · ·			
9494	2 Summary [LoE] POD_GF - Structural Works_Slab (excl. FG/5-7)	60	24-Sep-18	05-Dec-18	0												
9495 9496	[LoE] POD_GF - Structural Works_Slab_FG/5-7 [LoE] POD_GF - Structural Works_Walls	42 138	26-Mar-19 06-Nov-18	15-May-19 25-Apr-19	3 35												
9497 9520	[LoE] POD_GF - Structural Works_Staircases [LoE] POD_GF_Z02_Toilets/BoH/Corr/Lob - MEP Works	131 207	04-Dec-18 15-Feb-19	16-May-19 22-Oct-19	84 97					· · · · · · · · · · · · · · · · · · ·							
9523 9524	[LoE] POD_GF_Z02_Toilets/BoH/Corr/Lob - ABWF Works [LoE] POD_GF_Z03_Museum Shop & BoH - MEP Works	237 105	28-Jan-19 29-Apr-19	14-Nov-19 31-Aug-19	183 78			· · · · · · ·	-! !	·	++ 1 :						
9525	[LoE] POD_GF_Z03_Museum Shop & BoH - ABWF Works	148	15-Apr-19	10-Oct-19	213					· · · · · · · · · · · · · · · · · · ·							
9526 9527	[LoE] POD_GF_Z07_FoH Main Lobby - MEP Works [LoE] POD_GF_Z07_FoH Main Lobby - ABWF Works	141 231	30-Mar-19 09-Mar-19	16-Sep-19 11-Dec-19	30 160				-i i	·	÷						
9528 9529	[LoE] POD_GF_Z08 & GF_Z04_Ext Perimeter & Courtyard - MEP Works [LoE] POD_GF_Z08 & GF_Z04_Ext Perimeter & Courtyard - ABWF Works	96 158	25-Jul-19 18-May-19	16-Nov-19 23-Nov-19	15 175			: : 🗖	• •		· ·						
9530 9531	[LoE] POD_GF_Z09_Temp Exh. & BoH Surrounding - MEP Works [LoE] POD_GF_Z09_Temp Exh. & BoH Surndg - ABWF Works (Drying w/ Wild Air r	160 191	20-Apr-19 07-Mar-19	30-Oct-19 23-Oct-19	30 96				;		++						
9532	[LoE] POD_GF_Z09_Temp Exh. & BoH Sumdg - ABWF Works (Drying w/ Wild Air r	37	18-Nov-19	31-Dec-19	144					· · · · · · · · · · · · · · · · · · ·	++						
Level 1 Level 2	2 Summary																
9533 9534	[LoE] POD_L1 - Structural Works [LoE] POD_L1_Museum Shop Offices/Store/Lob - MEP Works	113 73	30-Oct-18 03-May-19	19-Mar-19 29-Jul-19	90 107		++			· · · · · · · · · · · · · · · · · · ·		·	·	-			
9535	[LoE] POD_L1_Museum Shop Offices/Store/Lob - ABWF Works	121	11-Apr-19	02-Sep-19	243					;							
Level 11	MF 2 <i>Summary</i>																
9536 9537	[LoE] POD_1M - Structural Works [LoE] POD_1M_Z01 to 1M_Z04_MEP Plant Rms/Lob/Corr - MEP Works	95 227	24-Oct-18 26-Feb-19	20-Feb-19 25-Nov-19	83 2			· · · · · · · · · · · · · · · · · · ·	······		÷÷	××××××××××××					
9537 9538	[LoE] POD_1M_201 to 1M_204_MEP Plant Rms/Lob/Corr - MEP Works [LoE] POD_1M_Z01 to 1M_Z04_MEP Plant Rms/Lob/Corr - ABWF Works	329	26-Feb-19 06-Dec-18	25-Nov-19 13-Jan-20	134						++						
	▼ ▼ Milestone Current - Fcd Works Current - Other Works ⊠ Critical Works	CMW		-) 10 Sep 2018 Targ			19)	Date 28-Jan-19	CMV	Revisi WP Rev. 0 - Submiss	-		cked A BG	Approve à	эd
50	Current - Struct Works Current - MEP Works		ı arget F	rogramn	ne - L	evel 2 Summ	ary Bar Ch	art								_	
	Current - ABWF Works																

D Activity		ining Works @ 1 Start Finis		arget Program	(Rev_0; 28Jan19) -	CMWP_R0_1 201	9	 202	•	e 2 / 4
				Qtr 4 p Oct Nov [Qtr 1 Dec Jan Feb Mar	Qtr 2	Qtr 3	Qtr 1	Qtr 2	Qtr 3 Jul
Level 2 Level 2 Summary								 		
9543[LoE] POD_L2 - Structural Works9547[LoE] POD_L2_Z01_Temp Exh/Gal/BoH/Lob/Corr - MEP Works9548[LoE] POD_L2_Z01_Temp Exh/Gal/BoH/Lob/Corr - ABWF Wrks (Drying w/ Wild Air9549[LoE] POD_L2_Z01_Temp Exh/Gal/BoH/Lob/Corr - ABWF Wrks (Drying w/ Wild Air9550[LoE] POD_L2_Z02_Gal/BoH/Lob/Corr - MEP Works9551[LoE] POD_L2_Z02_Gal/BoH/Lob/Corr - ABWF Wrks (Drying w/ Wild Air not req'd)9552[LoE] POD_L2_Z02_Gal/BoH/Lob/Corr - ABWF Wrks (Drying w/ Wild Air req'd)9553[LoE] POD_L2_Z03_Gal/BoH/Lob/Corr - MEP Works9554[LoE] POD_L2_Z03_Gal/BoH/Lob/Corr - ABWF Wrks (Drying w/ Wild Air not req'd)	199 26- 201 13- 81 23- 209 21- 211 14- 130 18- 210 16-	Oct-18 25-Mar Feb-19 23-Oct Feb-19 12-Oct Dec-19 06-Apr Mar-19 27-Nov Mar-19 22-Nov Nov-19 28-Apr Mar-19 23-Nov Mar-19 17-Dec	-19 36 -19 205 -20 70 -19 6 -19 176 -20 51 -19 9							
9555 [LoE] POD_L2_Z03_Gal/BoH/Lob/Corr - ABWF Wrks (Drying w/ Wild Air req'd) 9557 [LoE] POD_L2_Z04_Gal/BoH/Lob/Corr - ABWF Wrks (Drying w/ Wild Air not req'd) 9558 [LoE] POD_L2_Z04_Gal/BoH/Lob/Corr - ABWF Wrks (Drying w/ Wild Air not req'd) 9559 [LoE] POD_L2_Z04_Gal/BoH/Lob/Corr - ABWF Wrks (Drying w/ Wild Air not req'd) 9559 [LoE] POD_L2_Z04_Gal/BoH/Lob/Corr - ABWF Wrks (Drying w/ Wild Air req'd) 9560 [LoE] POD_L2_Z05_Plaza - MEP Works 9561 [LoE] POD_L2_Z05_Plaza - ABWF Works Level L3 Lagendary	91 21- 207 23- 250 19- 150 18- 108 08	Jan-20 15-May Mar-19 27-Nov Mar-19 14-Jan Nov-19 22-May -Jul-19 14-Nov Jun-19 20-Jan	-20 37 -19 66 -20 133 -20 31 -19 18							
Level 2 Summary9562[LoE] POD_L3 - Structural Works9563[LoE] POD_L3_Z01 & L3_Z02 - MEP Works9564[LoE] POD_L3_Z01 & L3_Z02 - ABWF Works9751[LoE] POD_L3_Hard & Soft Landscaping incl MEP Works	159 19- 201 25-	Oct-18 22-May Apr-19 29-Oct Mar-19 22-Nov Mar-19 17-Feb	-19 32 -19 177							
EWS (External Wall System) Level 2 Summary										
1210 [LoE] POD_EWS_1MF - Podium Level 1MF Install Facade 8049 [LoE] POD_EWS_L2 - Podium Level 2 Install Facade 9565 [LoE] POD_EWS_B1F - Pisa South Peri_Install GW 9566 [LoE] POD_EWS_GF - Pisa Ceramic Tube Wall/GW w/ Ceramic Mullion Install 9567 [LoE] POD_EWS_2F_BF/11-13 - Pisa_East/West_Install GW 9568 [LoE] POD_EWS_3F- Skylight/Shop Front Glazing/Garden Roof & Wall Install 9569 [LoE] POD_EWS_GF- Corrugated Alum Perforated Panels Vertical Tra nspor ta tion Level 2 Summary	139 18- 110 04- 60 08- 72 03 154 01-	Oct-18 25-Jul Dec-18 10-Jun May-19 11-Sep Jun-19 17-Aug -Jul-19 25-Sep Mar-19 02-Sep Apr-19 24-Dec	-19 13 -19 1 -19 18 -19 118 -19 118							
9752 [LoE] POD_Verti_ Transport_Lift - Fireman's Lift 9753 [LoE] POD_Verti_ Transport_Lift - Other Lift		Dec-18 05-Jun Jan-19 14-Aug						 		
9754 [LoE] POD_Verti_ Transport_Esc - Escalators Risers Level 2 Summary		May-19 29-Nov	-19 64							· · · · · · · · · · · · · · · · · · ·
9570 [LoE] POD_Risers (Stg 1_Duct 1/2/3/5) 9787 [LoE] POD_Risers (Stg 2_Duct 4)		Nov-18 22-Apr -Jul-19 12-Sep								
Staircases Level 2 Summary										
9761 [LoE] POD_Staircases - Not Required for Pressurisation 9762 [LoE] POD_Staircases - Required for Pressurisation		-Apr-19 28-Oct -Apr-19 22-Oct								
M+ TOWER Construction										
Level 4										
Level 2 Summary 9851 [LoE] TW_L4 - Rem Structural Works (ST-02/02A) 6562 [LoE] TW_L4 - MEP Works (exd other prelim works) 6561 [LoE] TW_L4 - ABWF Works (excl wet trades or other prelim works) Level 5	98 01-	Nov-18 21-Nov Jun-19 26-Sep Apr-19 30-Oct	-19 21							
Level 2 Summary 6546 [LoE] TW_L5 - MEP Works (exd other prelim works)	135 30-	-Apr-19 10-Oct	-19 99						·	
6545 [LoE] TW_L5 - ABWF Works (excl wet trades or other prelim works) Level 6 Level 2 Summary		Apr-19 31-Oct								
6559 [LoE] TW_L5 - MEP Works (exd other prelim works) 6558 [LoE] TW_L6 - ABWF Works (excl wet trades or other prelim works) Level 7 Level 2 Summary		Feb-19 08-Nov Apr-19 18-Nov								· · · · · · · · · · · ·
6557 [LoE] TW_L7 - MEP Works (exd other prelim works) 6556 [LoE] TW_L7 - ABWF Works (excl wet trades or other prelim works) Level 8 Level 2 Summary	178 23	Feb-19 13-Nov Apr-19 22-Nov	-19 70							
6555 [LoE] TW_L8 - MEP Works (exd other prelim works) 6554 [LoE] TW_L8 - ABWF Works (excl wet trades or other prelim works) Level 9 Level 2 Summary		Feb-19 19-Nov Apr-19 28-Nov								· · · · · · · · · · · · · · · · · · ·
6553 [LoE] TW_L9 - MEP Works (exd other prelim works) 6552 [LoE] TW_L9 - ABWF Works (excl wet trades or other prelim works) Level 10 Level 2 Summary		Feb-19 28-Nov Apr-19 07-Dec								
6551 [LoE] TW_L10 - MEP Works (excl other prelim works) 6550 [LoE] TW_L10 - ABWF Works (excl wet trades or other prelim works) Level 11 Level 2 Summary		Feb-19 28-Nov Feb-19 07-Dec								
6548 [LoE] TW_L11 - MEP Works (excl other prelim works) 6547 [LoE] TW_L11 - ABWF Works (excl wet trades or other prelim works)		Feb-19 26-Nov Feb-19 06-Dec				· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·			
Level 12 Level 2 Summary								 		
6563 [LoE] TW_L12 - Structural Works (ST-02/02a) 6565 [LoE] TW_L12 - MEP Works (excl other prelim works)		-Oct-18 05-Nov Feb-19 03-Dec					· · · · · · · · · · · · · · · · · · ·			
6564 [LoE] TW_L12 - ABWF Works (excl wet trades or other prelim works) Level 13 Level 2 Summary	255 11-	Feb-19 12-Dec								· · · · · · · · · · · · · · · · · · ·
6566 [LoE] TW_L13 - Structural Works (ST-02/02a) 6568 [LoE] TW_L13 - MEP Works (excl other prelim works) 6567 [LoE] TW_L13 - ABWF Works (excl wet trades or other prelim works) Level 14	242 26-	Nov-18 26-Nov Feb-19 12-Dec Mar-19 21-Dec	-19 50							
Level 2 Summary 6569 [LoE] TW_L14 - Structural Works (ST-03, 02, 02a) 6572 [LoE] TW_L14 - MEP Works 6570 [LoE] TW_L14 - ABWF Works (excl wet trades or other prelim works) Level 15	242 26-	Nov-18 17-Dec Feb-19 12-Dec Mar-19 21-Dec	-19 50							
Level 2 Summary 6573 [LoE] TW_L15 - Structural Works (ST-02/02a/03 & East Core Rem Structure)	61 29	-Oct-18 09-Jan	-19 161							
6575 [LoE] TW_L15 - MEP Works 6574 [LoE] TW_L15 - ABWF Works (excl wet trades or other prelim works) Level 16 Level 2 Summary	225 26-	Feb-19 23-Nov Mar-19 03-Dec	-19 67							
6576 [LoE] TW_L16 - Structural Works (Rem Superstructure & Stair Cases) 6578 [LoE] TW_L16 - MEP Works		-Oct-18 14-Jan Feb-19 09-Nov								
6578 [LoE] TW_L16 - MEP Works 6577 [LoE] TW_L16 - ABWF Works (excl wet trades or other prelim works) Level RF Level 2 Summary		Heb-19 09-Nov Apr-19 19-Nov								
6579 [LoE] TW_RF - Structural Works (Rem Super-structure Works) 6581 [LoE] TW_RF - MEP Works	183 29-	Oct-18 14-Jan Jan-19 11-Sep	-19 118			·····		 		
6580 [LoE] TW_RF - ABWF Works	192 19-	Feb-19 09-Oct	-19 109							

Activity	OD	Start	Finish	TF		Qtr 4	Qtr 1		019	Otr 4		2020	2
					p Oct		Dec Jan Feb Mar A	Qtr 2 pr May Jur	Qtr 3 Jul Aug Sep O	Qtr 4 ct Nov Dec	Qtr 1 c Jan Feb Ma	Qtr Ir Apr Ma	
Level 2 Summary 6583 [LoE] TW_URF - Structural Works	75	31-Oct-18	29-Jan-19	34		+			+				
6583 [LOE] TW_URF - Structural Works 9857 [LoE] TW_URF - MEP Works	75 48	27-Jul-19	29-Jan-19 23-Sep-19	43		++							
WS (External Wall System)						++							
Level 2 Summary 4246 [LoE] TW_EWS - Facade Erection (Super Structure Weather Tight Phase)	187	12-Oct-18	31-May-19	29		++							
9858 [LoE] TW_EWS - Facade Erection (Super Structure Weather hight Phase)	75	31-May-19	29-Aug-19	141					- <u>-</u>				
ertical Transportation													
Level 2 Summary 4247 [LoE] TW_Lift - Lifts Install (Shaft & Lift Works Summarised)	208	15 Jan 10	26-Sep-19	117									
lisers	208	15-Jan-19	20-3ep-19	117		++							
Level 2 Summary						+ + + + + + +		¹ , ¹ ,		·			
1234 [LoE] TW_Riser - Risers	120	15-Dec-18	16-May-19	95									
taircases						++							
Level 2 Summary 4248 [LoE] TW_ST - ST02a and ST02 ABWF & MEP Works	93	24-Jan-19	21-May-19	224		$\frac{1}{7}$ $\frac{1}{7}$							
9859 [LoE] TW_ST - ST02a and ST02 Finishing Works	22	11-Jul-19	05-Aug-19	161									
9860 [LoE] TW_ST - ST01 and ST03 ABWF & MEP Works	74	18-Jul-19	16-Oct-19	103		<u> </u> <u>+</u> <u>+</u>							
F BUILDING													
evel GF			,	_									
Level 2 Summary													
9861 [LoE] CSF_GF - Rem Parapet Wal, Struct Remedial Works	36	21-Jan-19	09-Mar-19	79		ii i				·			
5790 [LoE] CSF_GF - MEP Works5789 [LoE] CSF_GF - ABWF Works (excl wet trades / other prelim works)	102 145	13-May-19 18-Mar-19	10-Sep-19 06-Sep-19	144 165									
9862 [LoE] CSF_GF - ABWF Works (Excl wer trades / other plenth works)	23	22-Jan-20	25-Feb-20	30		++							
evel 1						·+ · · · · · · · · · · · · · · · · · · ·							
Evel 2 Summary		00.01115	04 D: 10	000	<u>-</u> -	· · · · · · · · · · · · · · · · · · ·				·			
5501 [LoE] CSF_L1 - MEP Works (early works) 9864 [LoE] CSF_L1 - MEP Works	56 174	20-Oct-18 17-Jan-19	24-Dec-18 19-Aug-19	233 71		4 4			<u></u>				
5500 [LoE] CSF_L1 - ABWF Works (excl wet trades / other prelim works)	144	07-Mar-19	26-Aug-19	175	 -;	$\frac{1}{1} = \frac{1}{1}$ $\frac{1}{1} = \frac{1}{1}$							
evel 2						¦			+				
Level 2 Summary 5731 [LoE] CSF_L2 - MEP Works (early works)	56	20-Oct-18	24-Dec-18	232	<u>-</u> -	; ; ;				·			
9865 [LoE] CSF_L2 - MEP Works	150	26-Feb-19	23-Aug-19	79	1				-;;;;;;;				
5730 [LoE] CSF_L2 - ABWF Works (excl wet trades / other prelim works)	168	12-Feb-19	30-Aug-19	171		+ 							
evel 3 Level 2 Summary													<u>-</u>
5677 [LoE] CSF_L3 - MEP Works (early works)	56	20-Oct-18	24-Dec-18	233		<u></u>			······				
9867 [LoE] CSF_L3 - MEP Works	174	17-Jan-19	19-Aug-19	101									
5676 [LoE] CSF_L3 - ABWF Works (excl wet trades / other prelim works) evel 4	140	12-Mar-19	26-Aug-19	175									
Level 2 Summary						++			+				
5621 [LoE] CSF_L4 - MEP Works	106	26-Apr-19	30-Aug-19	61	1	+ + + + + + + + + + + + + + +							
5620 [LoE] CSF_L4 - ABWF Works (excl wet trades / other prelim works) evel 5	127	09-Apr-19	06-Sep-19	165									
evel 5 Level 2 Summary						· · · · · · ·			+				
5502 [LoE] CSF_L5 - Structural Works (ST-52)	18	29-Oct-18	17-Nov-18	154									
5566 [LoE] CSF_L5 - MEP Works	106	26-Apr-19	30-Aug-19	73									
5565 [LoE] CSF_L5 -ABWF Works (excl wet trades / other prelim works) evel 6	115	23-Apr-19	06-Sep-19	165		++							
Level 2 Summary						++							
5791 [LoE] CSF_L6 - Structural Works	29	06-Nov-18	08-Dec-18	154				<u>-</u>					
5849 [LoE] CSF_L6 - MEP Works 5848 [LoE] CSF_L6 - ABWF Works (excl wet trades / other prelim works)	119 137	26-Apr-19 23-Apr-19	16-Sep-19 04-Oct-19	48 143									
evel 7	10,	2070110	0100010	110		<u>+</u> <u>+</u>							
Level 2 Summary													
5850 [LoE] CSF_L7 - Structural Works (Perim. Wall to 8/F) 9868 [LoE] CSF_L7 - Structural Works (ST-52)	38 18	12-Oct-18 22-Feb-19	26-Nov-18 14-Mar-19	170 98		;;							
6105 [LoE] CSF_L7 - MEP Works	173	26-Apr-19	20-Nov-19	9		++		*******					
6104 [LoE] CSF_L7 - ABWF Works (excl wet trades / other prelim works)	188	23-Apr-19	04-Dec-19	92									
evel 8 & Roof Level Level 2 Summary										·			
6255 [LoE] CSF_L8 - Structural Works	124	12-Oct-18	15-Mar-19	31		<u></u>		 					
6257 [LoE] CSF_L8 - MEP Works	237	31-Jan-19	18-Nov-19	8		+ + + + +		*****		×××××			
6256 [LoE] CSF_L8 - ABWF Works WS (External Wall System)	241	16-Feb-19	02-Dec-19	94									
Level 2 Summary						++							
3844 [LoE] CSF_L8_&_Roof - EWS (External Wall System)	177	20-Dec-18	27-Jul-19	42	1	·							
6331 [LoE] CSF_L8_&_Roof - Roof Waterpoofing & Panels ertical Transportation	153	15-Apr-19	16-Oct-19	30		· · · · · · · · · · · · · · · · · · ·			- I				
Level 2 Summary													
3845 [LoE] CSF_LT-51/LT-53	213	16-Mar-19	27-Nov-19	54		1 1 1			- <u>-</u> <u>+</u> <u>+</u> <u>+</u>	· · · · · · · · · · · · · · · · · · ·			
6163 [LoE] CSF_LT-52	118	10-Jul-19	27-Nov-19	54		$\frac{1}{1}$							
lisers Level 2 Summary													
3846 [LoE] CSF_RISERS - Risers MEP Works	142	12-Nov-18	07-May-19	125		++	iiiiiii						
taircases										·			
Level 2 Summary		4014	04.1.15	000					·				
6187 [LoE] CSF_ST - Stair Cases (ST51 & ST52) esting & Commissioning	80	18-Mar-19	21-Jun-19	230		++							
evel 2 Summary						1 1 1 1 1 1 1 1 1 1 1							
[LoE] Level 2 Summary - Wild Air Stage 1 T&C (1/F to 5/F)	96	15-Apr-19	07-Aug-19	130		++		 					
Image: 332[LoE] Level 2 Summary - Wild Air Stage 2 T&C (GF, 6/F to 8/F)Image: 433[LoE] Level 2 Summary - CSF MC T&C for FSD All Levels (major items)	46 36	09-Oct-19 05-Nov-19	30-Nov-19 16-Dec-19	34 50									
E BUILDING	30	00-1400-19	-0-Dec-19	- 50		++							
onstruction						<u>+</u> <u>+</u>				·			
evel GF													
Level 2 Summary					[[T T 							
6588 [LoE] RDE_GF - MEP Works 6587 [LoE] RDE_GF - ABWF Works	251 276	16-Jan-19 29-Dec-18	19-Nov-19 02-Dec-19	29 168		т + 							
6587 [LoE] RDE_GF - ABWF Works evel 1	210	20-Det-10	02-Dec-18	100	1								
Level 2 Summary						+ + 							L
6589 [LoE] RDE_L1 - Structural Works (late cast area)	5	02-Mar-19	07-Mar-19	112	- <u> </u>								
6591 [LoE] RDE_L1 - MEP Works 6590 [LoE] RDE_L1 - ABWF Works	321 347	29-Nov-18 10-Nov-18	26-Dec-19 08-Jan-20	16 138					-;;;;;				
evel 2						T T 							
Level 2 Summary						T T T				·			
6592 [LoE] RDE_L2 - Structural Works (late cast area)	5	25-Feb-19	01-Mar-19	13						·		, = = = = = = = = = = = = = =	
6595 [LoE] RDE_L2 - MEP Works 6594 [LoE] RDE_L2 - ABWF Works	259 287	01-Dec-18 10-Nov-18	16-Oct-19 29-Oct-19	58 198						.			L
evel 3										· • • • • • • • • • • • • • • • • • • •			
Level 2 Summary													
6596[LoE] RDE_L13 - Structural Works (late cast strip)6598[LoE] RDE_L13 - MEP Works	5 259	19-Feb-19 01-Dec-18	23-Feb-19 16-Oct-19	13 58			S		<u></u>				
6598 [LOE] RDE_L13 - MEP Works 6597 [LoE] RDE_L13 - ABWF Works	259	10-Nov-18	29-Oct-19	58 198	- <u> </u>								
					1-2-2-2	· + · ·							

Activity		OD	Start	Finish	TF	Qtr 4 Qtr 1 D Oct Nov Dec Jan Feb Mar	2019 Qtr 2 Apr May Jun Jul	Qtr 3 Aug Sep	Qtr 4	4 Qtr ⁻	1	020 Qtr 2 pr May	Jun
	DE_L4 - Structural Works (late cast strip) DE_L4 - MEP Works	5 271	13-Feb-19 01-Dec-18	18-Feb-19 30-Oct-19	13 46								
6600 [LoE] R	DE_L4 - ABWF Works	271	10-Nov-18	11-Nov-19	186			· • +	+				
Level 5 <i>Level 2 Summa</i>	ry												
6602 [LoE] R	DE_L5 - Structural Works (ST & late cast strip)	90	22-Oct-18	12-Feb-19	13		1 I I I 1 I I I		i i	· · · · · · · · · · · · · · · · · · ·			
6603 [LoE] R	IDE_L5 - MEP Works IDE_L5 - ABWF Works	277 294	23-Nov-18 10-Nov-18	29-Oct-19 05-Nov-19	47 191		; ; ; ; ; ;	·					
∟evel 6 <i>Level 2 Summa</i>	rv								 	· · · · · · · · · · · · · · · · · · ·			
6584 [LoE] R	DE_L6 - Structural Works (ST & Late Cast Strip)	67	12-Nov-18	30-Jan-19	13				+				
	DE_L6 - MEP Works DE_L6 - ABWF Works	233 294	16-Jan-19 10-Nov-18	29-Oct-19 05-Nov-19	47 191		· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·					
Level 7													
Level 2 Summa 6606 [LoE] R	DE_L7 - Structural Works (ST & Late Cast Strip)	44	03-Dec-18	24-Jan-19	13			· · · · · · · · · · · · · · · · · · ·		· · · · · · · · · · · · · · · · · · ·			
	DE_L7 - MEP Works DE_L7 - ABWF Works	245 281	16-Jan-19 10-Dec-18	12-Nov-19 19-Nov-19	35 179		· · · · · · · · · · · · · · · · · · ·		<u>.</u>				
Level 8									*	· · · · · · · · · · · · · · · · · · ·			
Level 2 Summa 6609 [LoE] R	ry DE_L8 - Structural Works (Rem Slab/Columns; ST & Late Cast Strip)	82	12-Oct-18	18-Jan-19	176				i i i +				
	DE_L8 - MEP Works DE_L8 - ABWF Works	244 261	17-Jan-19 04-Jan-19	12-Nov-19 19-Nov-19	35 179				·				
_evel 9				10110110					+				
6612 [LoE] R	ry DE_L9 - Structural Works, ST & Staircases	78	05-Nov-18	12-Feb-19	89				· · · · · · · · · · · · · · · · · · ·				
6614 [LoE] R	DE_L9 - MEP Works DE_L9 - ABWF Works	223 240	18-Feb-19 29-Jan-19	12-Nov-19 19-Nov-19	35 179			· · · · · · · · · · · · · · · · · · ·	+	· · · · · · · · · · · · · · · · · · ·			
_evel 10		240	25-0411-15	13110713	175								
Level 2 Summa 6616 [LoE] R	ry IDE L10 - Structural Works & Staircases	78	28-Nov-18	07-Mar-19	87								
6617 [LoE] R	DE_L10 - ABWF Works	223	01-Mar-19	23-Nov-19	175		·····	· · · · · · · · · · · · · · · · · · ·	+				
6618 [LoE] R .evel 11	DE_L10 - MEP Works	206	14-Mar-19	16-Nov-19	31								
Level 2 Summa		70	22 Dec 10	01 0= 10	0.4				, , , , , , , , , , , , , , , , ,				
6621 [LoE] R	DE_L11 - Structural Works & Staircases DE_L11 - MEP Works	78 185	22-Dec-18 09-Apr-19	01-Apr-19 16-Nov-19	84 31			· · · · · · · · · · · · · · · · · · ·					
6620 [LoE] R _evel 12	DE_L11 - ABWF Works	202	26-Mar-19	23-Nov-19	175								
Level 2 Summa							· · · · · · · · · · · · · · · · · · ·		+			·····	
	DE_L12 - Structural Works & Staircases DE_L12 - MEP Works	88 133	18-Jan-19 16-May-19	09-May-19 23-Oct-19	71 52			· · · · · · · · · · · · · · · · · · ·	<u>.</u>				
	DE_L12 - ABWF Works	154	03-May-19	05-Nov-19	192			· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·				
Level 2 Summa									1 1 +				
	DE_L13 - Needle Beam, Structural Works & Staircases DE_L13 - MEP Works	88 125	19-Feb-19 11-Jun-19	03-Jun-19 07-Nov-19	68 39								
6627 [LoE] R	DE_L13 - ABWF Works	146	28-May-19	20-Nov-19	179				<u> </u>				
.evel 14 <i>Level 2 Summa</i>	ry												
6629 [LoE] R	DE_L14 - Structural Works & Staircases DE_L14 - MEP Works	67 122	06-Apr-19 06-Jul-19	25-Jun-19 28-Nov-19	68 21								
6630 [LoE] R	DE_L14 - MEP Works DE_L14 - ABWF Works	122	22-Jun-19	11-Dec-19	161	↓ - ↓ + → ↓ + → + → + → + → + → + → + → + → + → + → + → + → + → + → + → + → + → - + + → - + → - + → - + + → - + → - + + → - + + → - + + → - + + → - + + → - + + → - + + + → - + + + → - + + + → - + + + +		-	+				
.evel 15 <i>Level 2 Summa</i>	ry							· · · · · · · · · · · · · · · · · · ·					
6632 [LoE] R	DE_L15 - Structural Works & Staircases	94	22-Apr-19	12-Aug-19	46	↓	· · · · · · · · · · · · · · · · · · ·		· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·			
6633 [LoE] R	DE_L15 - MEP Works DE_L15 - ABWF Works	101 117	17-Aug-19 06-Aug-19	16-Dec-19 23-Dec-19	24 150				+				
₋evel 15 WF <i>Level 2 Summa</i>	rv												
6635 [LoE] R	DE_L15MF - Needle Beam, Struct'l Works & Staircases	61	24-May-19	05-Aug-19	29			<mark>_</mark>	i i +				
6636 [LoE] R	DE_L15MF - MEP Works DE_L15MF - ABWF Works	99 129	21-Sep-19 10-Sep-19	18-Jan-20 20-Feb-20	3 108								
_evel 15M/F UF &	& RF												
	DE_L15MF UF & RF - Structural Works	60	02-Jul-19	09-Sep-19	0								
6641 [LoE] R	DE_L15MF UF & RF - MEP Works DE_L15MF UF & RF - ABWF Works	30 54	09-Nov-19 19-Oct-19	13-Dec-19 20-Dec-19	14 146								
WS (External W	_								+	· · · · · · · · · · · · · · · · · · ·			
L2 Summary 3835 [LoE] R	DE_FCD - EWS Facade Install to Weather Tight Stage to Roof LvI	347	27-Dec-18	02-Mar-20	99								
ertical Transpo	rtation												
Level 2 Summa 5413 [LoE] R	ry IDE_FCD - Lifts	276	19-Jan-19	21-Dec-19	22			· · · · · · · · · · · · · · · · · · ·					
	DE_FCD - Escalators	127	02-Feb-19	11-Jul-19	216								
lisers <i>Level 2 Summa</i>	ry												
1235 [LoE] R Staircases	DE_Duct_D - Electrical Riser Duct	127	24-May-19	24-Oct-19	21				 				
Level 2 Summa	ry												
	DE_ST - Staircases ST-71/72 DE_ST - Staircases ST-73/74	92 92	10-Dec-18 12-Aug-19	04-Apr-19 29-Nov-19	368 170					3			
esting & Con	nmissioning						· · · · · · · · · · · · · · · · · · ·						
.evel 2 Summar 7642 [LoE] R	y IDE - T&C (early works)	104	15-Nov-19	25-Mar-20	25								
7672 [LoE] R	DE - T&C (back end works)	78	26-Mar-20	25-Mar-20 27-Jun-20	1				+				***
TERNAL WO													
evel 2 Summar	у												
9873 [LoE] IC	- CP_REM - Interfacing Carpark Misc. Works PA_Portion 1 - External Works	16 57	12-Oct-18 10-Oct-18	31-Oct-18 15-Dec-18	0 228				T				
9879 [LoE] IF	PA_Portion 2 - External Works	56	23-Oct-18	27-Dec-18	445		· · · · · · · · · · · · · · · · · · ·		+ + +				
9881 [LoE] IF	PA_Portion 3 - External Works PA_Portion 4 - External Works	56 84	23-Oct-18 10-Oct-18	27-Dec-18 18-Jan-19	445 427				; ; ; ; ;				
	PA_300T Crane Area - External Works long Building Boundary - External Works	69 371	19-Nov-18 20-Oct-18	15-Feb-19 15-Jan-20	409 26				+				
9883 [LoE] P	romenade - External Works	39	23-Oct-18	06-Dec-18	462					· · · · · · · · · · · · · · · · · · ·			
	STATUTORY INSPECTIONS & APPROVALS dium, M+ Tower & CSF Building												
SD & BD													
	SD Inspection/Re-Inspection/Remedial Works - Advanced Layout Inspection SD Inspection/Re-Inspection/Remedial Works - FS SYSTEMS INSPECTION	26 72	13-Nov-19 19-Dec-19	12-Dec-19 23-Mar-20	5 0				<u>+</u>				
BD BD - Ins	spection/Re-Inspection otain OP for Basement/Podium/M+/CSF	24	24-Feb-20 23-Mar-20	23-Mar-20 30-Mar-20	0				+		××××		
DE Building		0			0				, 1 +				
SD & BD	SD - ESD Inspection/Do Inspection/Demodial Market (Inspects 2 and 1)	40	00 Ect 00	24 4== 22	0				,				
RDE_BD RDE_B	SD - FSD Inspection/Re-Inspection/Remedial Works (layouts & systems) D - Inspection/Re-Inspection	48 24	28-Feb-20 25-Apr-20	24-Apr-20 23-May-20	0								
7490 RDE_B	D - Obtain OP for RDE	6	25-May-20	30-May-20	0								

Lyric Theatre Complex

ric Theatre Complex (3MRP) - Enviromental avation and Lateral Support (ELS) Stage 2 Works (Stage 2) 1: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 2: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 3: Area 3: Install Waling & Strut Layer S4 3 Excavate to Formation Level -9.6mPD	26-Apr-19 A 29-Apr-19 A 16-Jan-19 A	22-May-19 25-May-19*	Apr 16	May 17	Jun 18	Jul 19
avation and Lateral Support (ELS) Stage 2 Works (Stage 2) 1: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 2: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 3: Area 3: Install Waling & Strut Layer S4	29-Apr-19 A 16-Jan-19 A	25-May-19*			18	
avation and Lateral Support (ELS) Stage 2 Works (Stage 2) 1: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 2: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 3: Area 3: Install Waling & Strut Layer S4	29-Apr-19 A 16-Jan-19 A	25-May-19*				
Works (Stage 2) 1: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 2: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 3: Area 3: Install Waling & Strut Layer S4	29-Apr-19 A 16-Jan-19 A	25-May-19*				
1: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 2: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 3: Area 3: Install Waling & Strut Layer S4	29-Apr-19 A 16-Jan-19 A	25-May-19*				
2: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 3: Area 3: Install Waling & Strut Layer S4	29-Apr-19 A 16-Jan-19 A	25-May-19*				
2: Excavate to -9.0, -11.3, -14.2 w/ soil Berm 3: Area 3: Install Waling & Strut Layer S4	29-Apr-19 A 16-Jan-19 A	25-May-19*			ا ا ۲	
3: Area 3: Install Waling & Strut Layer S4	16-Jan-19 A	,				
3: Area 3: Install Waling & Strut Layer S4	16-Jan-19 A	,				
		13-Apr-19 A				
S Excavate to Formation Level -9.6mPD						,
	18-Apr-19 A	22-May-19				
4. Europeato to 10 1 m PD	17 Jan 10 A	10 Arr 10 A				
4: Excavate to -6.1mPD	17-Jan-19 A	12-Apr-19 A				
4: Install Waling & Strut Layer S4	16-Feb-19A	15-Apr-19A				
4: Excavate to Formation Level -9.6mPD	23-May-19	21-Jun-19*				
ement						
sential Basement Structure (Excl. AET Protection & Box Culvert)						
1 - L01] Blinding Layer for Pile Cap / B2 Slab at Central Portion	11-May-19	17-Jun-19				
1 - L01] Construct Central Pile Cap / B2 Slab at -11.3mPD & -14.2mPD	17-May-19	18-Jul-19				
ı - L04] Blinding Layer for Pile Cap / B2 Slab	19-Jun-19	24-Jul-19				
I - L04] Construct Pile Cap / B2 Slab at -9.6mPD	21-Jun-19	21-Aug-19				
6 - L06] Construct B1-B1M Columns & Structural Walls	10-Dec-18 A	10-May-19				
6 - L06] Construct B1M Beam & Slab	14-Jan-19 A	16-May-19				
6 - L06] Remove Strut Laver S1	18-Feb-19A	25-Apr-19 A				
	17-Mav-19					
-	-					
· · · · · · · · · · · · · · · · · · ·						
	13-Mar-19 A	08-Apr-19A				
					· · · · · · · · · · · · · · · · · · ·	
	-	,				
	17-May-19	14-Jun-19		1		
	4: Excavate to Formation Level -9.6mPD ement sential Basement Structure (Excl. AET Protection & Box Culvert) n - L01] Blinding Layer for Pile Cap / B2 Slab at Central Portion n - L01] Construct Central Pile Cap / B2 Slab at -11.3mPD & -14.2mPD n - L04] Blinding Layer for Pile Cap / B2 Slab n - L04] Construct Pile Cap / B2 Slab at -9.6mPD 6 - L06] Construct B1-B1M Columns & Structural Walls 6 - L06] Construct B1-B1M Columns & Structural Walls 6 - L06] Construct B1M Beam & Slab 6 - L06] Construct B1M-GF Columns & Structural Walls 6 - L06] Construct GF Beam & Slab (South & Northeast) Works for Artist Square Bridge r ruct Bored Pile BP-1 ruct Bored Pile BP-4 ace Core & Sonic Tests it As-built Record & Select Test Pile Project ID: West Kowloon (Section 1)	4: Excavate to Formation Level -9.6mPD23-May-19ementsential Basement Structure (Excl. AET Protection & Box Culvert)n - L01] Blinding Layer for Pile Cap / B2 Slab at Central Portion11-May-19n - L01] Construct Central Pile Cap / B2 Slab at -11.3mPD & -14.2mPD17-May-19n - L04] Blinding Layer for Pile Cap / B2 Slab at -9.6mPD21-Jun-19n - L04] Construct Pile Cap / B2 Slab at -9.6mPD21-Jun-196 - L06] Construct B1-B1M Columns & Structural Walls10-Dec-18 A6 - L06] Construct B1M Beam & Slab14-Jan-19 A6 - L06] Construct B1M Beam & Slab17-May-196 - L06] Construct GF Beam & Slab (South & Northeast)08-Jun-19Works for Artist Square Bridgerruct Bored Pile BP-113-Mar-19 Aace Core & Sonic Tests02-May-19it As-built Record & Select Test Pile	4: Excavate to Formation Level -9.6mPD23-May-1921-Jun-19*ementsential Basement Structure (Excl. AET Protection & Box Culvert)n - L01] Blinding Layer for Pile Cap / B2 Slab at Central Portion11-May-1917-Jun-19n - L01] Construct Central Pile Cap / B2 Slab at -11.3mPD & -14.2mPD17-May-1918-Jul-19n - L04] Blinding Layer for Pile Cap / B2 Slab at -9.6mPD21-Jun-1924-Jul-19n - L04] Construct Pile Cap / B2 Slab at -9.6mPD21-Jun-1921-Aug-196 - L06] Construct B1-B1M Columns & Structural Walls10-Dec-18 A10-May-196 - L06] Construct B1M Beam & Slab14-Jan-19 A16-May-196 - L06] Construct B1M-GF Columns & Structural Walls17-May-1913-Jul-196 - L06] Construct GF Beam & Slab (South & Northeast)08-Jun-1903-Aug-19Works for Artist Square Bridgeruct Bored Pile BP-113-Mar-19 A08-Apr-19 Aaccore & Sonic Tests02-May-1916-May-19	4: Excavate to Formation Level -9.6mPD23-May-1921-Jun-19*ementsential Basement Structure (Excl. AET Protection & Box Culvert) L01] Blinding Layer for Pile Cap / B2 Slab at Central Portion11-May-1917-Jun-19 L01] Construct Central Pile Cap / B2 Slab at -11.3mPD & -14.2mPD17-May-1918-Jul-19 L04] Blinding Layer for Pile Cap / B2 Slab at -9.6mPD21-Jun-1924-Jul-19 L04] Construct Pile Cap / B2 Slab at -9.6mPD21-Jun-1921-Aug-19 L04] Construct B1-B1M Columns & Structural Walls10-Dec-18 A10-May-19 L06] Construct B1-B1M Columns & Structural Walls10-Dec-18 A10-May-19 L06] Construct B1M Beam & Slab14-Jan-19 A16-May-19 L06] Construct B1M-GF Columns & Structural Walls17-May-1913-Jul-19 L06] Construct GF Beam & Slab (South & Northeast)08-Jun-1903-Aug-19 Works for Artist Square Bridge	4: Excavate to Formation Level -9.6mPD 23-May-19 21-Jun-19* ement sential Basement Structure (Excl. AET Protection & Box Culvert) n - L01] Blinding Layer for Pile Cap / B2 Slab at Central Portion 11-May-19 17-Jun-19 n - L01] Construct Central Pile Cap / B2 Slab at Central Portion 11-May-19 18-Jul-19 n - L04] Blinding Layer for Pile Cap / B2 Slab at -11.3mPD & -14.2mPD 19-Jun-19 24-Jul-19 n - L04] Construct Pile Cap / B2 Slab at -9.6mPD 21-Jun-19 21-Aug-19 6 - L06] Construct B1-B1M Columns & Structural Walls 10-Dec-18A 10-May-19 6 - L06] Construct B1M Beam & Slab 14-Jan-19A 16-May-19 6 - L06] Construct B1M Ge Columns & Structural Walls 17-May-19 13-Jul-19 6 - L06] Construct GF Beam & Slab (South & Northeast) 08-Jun-19 03-Aug-19 6 - L06] Construct GF Beam & Slab (South & Northeast) 08-Jun-19 03-Aug-19 7 Truct Bored Pile BP-1 13-Mar-19A 08-Apr-19A 7 Truct Bored Pile BP-4 09-Apr-19A 09-Apr-19A 4 - Core & Sonic Tests 02-May-19 16-May-19 16-May-19	4: Excavate to Formation Level -9.6mPD 23-May-19 21-Jun-19* ement 23-May-19 21-Jun-19* sential Basement Structure (Excl. AET Protection & Box Culvert) 1 1 1 - L01] Blinding Layer for Pile Cap / B2 Slab at Central Portion 11-May-19 17-Jun-19 1 - L01] Construct Central Pile Cap / B2 Slab at 1.13mPD & -14.2mPD 17-May-19 18-Jul-19 1 - L04] Blinding Layer for Pile Cap / B2 Slab at -9.6mPD 21-Jun-19 24-Jul-19 1 - L04] Construct Pile Cap / B2 Slab at -9.6mPD 21-Jun-19 21-Aug-19 6 - L06] Construct B1-B1M Columns & Structural Walls 10-Dec-18A 10-May-19 6 - L06] Construct B1M Beam & Slab 14-Jan-19A 16-May-19 6 - L06] Construct B1M-GF Columns & Structural Walls 17-May-19 13-Jul-19 6 - L06] Construct GF Beam & Slab (South & Northeast) 08-Jun-19 03-Aug-19 6 - L06] Construct GF Beam & Slab (South & Northeast) 08-Jun-19 03-Aug-19 7 7 7 7 7 7 7 7 7 7 7 7 8 - L06] Construct B1M-GF Columns & Structural Walls 17-May-19 13-Jul-19 7 7

Layout: L1-3MRP (Env)

Actual Work

Milestone

٠

L1 Contract for Lyric Theatre Complex & Extended Basement Three Month Rolling Programme (3MRP) - Status as of 30 Apr 2019



tivity ID	Activity Name	Start Date	Finish Date			019	
			-	Apr 16	May 17	Jun 18	Jul 19
CAI12270	Pile Test Set-up, Test & Remove	15-Jun-19	13-Jul-19	10	17	10	19
CAI12280	Pile Test Result Submission & Approval (HyD)	15-Jul-19	10-Aug-19		-		
Cost Centre D	- Public Infrastructure Works (PIW)				-		,
	02 - Austin Road West Lay-by						,·
	2.1 Roadworks and Remaining					·	,
MC30-Ch.1	70 to MC30-Ch.150		-				,
CD210730	MC30-Ch170-150: Roadworks & Footpath	30-Jan-19 A	16-May-19				·
CD210750	MC30-Ch170-150: Install Street Furniture & Lighting	17-May-19	06-Jun-19				·
MC30-Ch.1	50 to MC30-Ch.100						· · · · · · · · · · · · · · · · · · ·
CD210630	MC30-Ch150-100: Roadworks & Footpath	13-Feb-19A	30-May-19				·
CD210650	MC30-Ch150-100: Install Street Furniture & Lighting	08-Jun-19	28-Jun-19				·
MC30-Ch.1	00 to MC30-Ch.50						
CD210530	MC30-Ch100-50: Roadworks & Footpath	31-May-19	18-Jul-19			(
CD210535	MC30-Ch100-50: Maintenance Staircase	27-Jun-19	18-Jul-19				
CD210550	MC30-Ch100-50: Install Street Furniture & Lighting	19-Jul-19	08-Aug-19				
MC30-Ch.5	0 to MC30-Ch.00		-				,
CD210410	MC30-Ch50-00: Road Drainage (WL3.1 to WL1.12)	26-Jan-19 A	06-Jun-19				·
CD210420	MC30-Ch50-00: DN450 Freshwater (0+64 - 0+14)	08-Jun-19	13-Jul-19				
CD210425	MC30-Ch50-00: DN450 Salt Water (0+062 - 0+12)	25-Jun-19	30-Jul-19				
Cost Centre D	2.2 Drainage						,
MC20-Ch.14	40 to MC20-Ch.00						,
MC20-Ch.1	140 to MC20-Ch.120 (MH SF_1.2A_2 to SF_1.1)					'	; }
CD2201840	MC20-Ch140-00: 1800mm dia Drainage (SF1.2A_2 to SF1.1) - Excavation & Els	25-Jan-19 A	25-Apr-19 A				
	MC20-Ch140-00: 1800mm dia Drainage (SF1.2A_2 to SF1.1) - Install Drainage	26-Apr-19 A	04-May-19			'	
CD2201880	MC20-Ch140-00: 1800mm dia Drainage (SF1.2A_2 to SF1.1) - Construct Manhole	18-Apr-19 A	17-May-19				
MC20-Ch.1	120 to MC20-Ch.80 (MH SF_1.1 to SF_1.1A)					· · · · · · · · · · · · · · · · · · ·	
	MC20-Ch140-00: 1800mm dia Drainage (SF1.1 to SF1.1A)) - Sheet Pile	18-May-19	08-Jun-19				
zD2201840	MC20-Ch140-00: 1800mm dia Drainage (SF1.1 to SF1.1A) - Excavation & Els	01-Jun-19	22-Jun-19				
zD2201860	MC20-Ch140-00: 1800mm dia Drainage (SF1.1 to SF1.1A) - Install Drainage	18-Jun-19	02-Jul-19				2

Project ID: Remaining Work L13MRP-20190430-Env Critical Remaining Work Actual Work Milestone

٠

Layout: L1-3MRP (Env)

West Kowloon Cultural District Authority L1 Contract for Lyric Theatre Complex & Extended Basement Three Month Rolling Programme (3MRP) - Status as of 30 Apr 2019



C. Action and Limit Levels for Construction Phase

Air Quality

The Action and Limit Levels for 1-hour and 24-hour TSP for the monitoring station are presented in following tables:

Table C-1: Action and Limit Levels for 1-hour TSP							
Monitoring	J Station	Action Level (mg/m ³)	Limit Level (mg/m ³)				
AM	1	273.7	500				
AM2	2B	274.2	500				

Table C-2: Action and Limit Levels for 24-hour TSP

Monitoring Station	Action Level (µg/m³)	Limit Level (µg/m³)
AM1	143.6	260
AM2B	151.1	260

<u>Noise</u>

The Action and Limit Levels for Noise for the monitoring stations are presented in following table:

Table C-3: Action and Limit Levels for Construction Noise

Time Period & Monitoring Locations	Action Level	Limit Level
NM1A		
0700-1900 hours on normal weekdays	When one documented complaint is received from any one of the sensitive receivers	75 dB(A)

D. Event and Action Plan for Air Quality, Noise, Landscape and Visual Impact

Air Quality

In case the Action and Limit Levels are not complied during construction stage, the following Event and Action Plan should be followed:

Table D-1: Event and Action Pla	lan for	Air Quality
---------------------------------	---------	-------------

informed of the results.

Event		Action	า	
	ET	IEC	WKCDA	Contractor
Action Level				
1. Exceedance for one sample	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and WKCDA; Repeat measurement to confirm finding; Increase monitoring frequency to daily. 	 Check monitoring data submitted by ET; Check Contractor's working method. 	1. Notify Contractor	 Rectify any unacceptable practice; Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	 Identify source; Inform IEC and WKCDA; Advise the WKCDA on the effectiveness of the proposed remedial measures; Repeat measurements to confirm findings; Increase monitoring frequency to daily; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with IEC and WKCDA; If exceedance stops, cease additional monitoring. 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Monitor the implementation of remedial measures. 		 Submit proposals for remedial to WKCDA within three working days of notification; Implement the agreed proposals; Amend proposal if appropriate.
Limit Level	monitoring.			
1. Exceedance for one sample	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform WKCDA, Contractor and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and WKCDA informed of the results 	 Check Contractor's working method; Discuss with ET and Contractor on possible premedial measures; Advise the WKCDA on the effectiveness of the proposed remedial 	notification of failure in writing;	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within three working days of notification; Implement the agreed proposals; Amend proposal if appropriate.

Event

Action

2. Exceedance for two or more consecutive samples	 Notify IEC, WKCDA, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and WKCDA to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and WKCDA informed of the results; If exceedance stops, cease additional monitoring. 	 Discuss amongst WKCDA, ET, and Contractor on the potentia remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the WKCDA accordingly; Monitor the implementation of remedial measures 	notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree liwith the Contractor on the remedial measures to be implemented; 4. Ensure remedial	 action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within three working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the WKCDA until the exceedance is abated.

Construction Noise

In case the Action and Limit Levels are not complied during construction stage, the following Event and Action Plan should be followed:

Event	Action					
	ET	IEC	WKCDA	Contractor		
Action Level	 Notify WKCDA, IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, WKCDA and Contractor; Discuss with the IEC and Contractor on remedial measures required; Increase monitoring frequency to check mitigation effectiveness. 	investigation results	in writing;2. Notify Contractor;3. In consolidation with the IEC, agree with the Contractor	mitigation proposals to IEC and WKCDA;		
Limit Level	 Inform IEC, WKCDA, Contractor and EPD; Repeat measurements to confirm findings; Increase monitoring frequency; Identify source and investigate the cause of exceedance; Carry out analysis of Contractor's working procedures; Discuss with the IEC, Contractor and WKCDA on remedial measures required; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and WKCDA informed of the results; If exceedance stops, cease additional monitoring. 	 Discuss amongst WKCDA, ET, and Contractor on the potentia remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the WKCDA accordingly. 	 lin writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures; If exceedance continues, consider stopping the Contractor to 	 action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and WKCDA within 3 working days of notification; 3. Implement the agreed proposals; 4. Submit further proposal if problem still not under control; 5. Stop the relevant portion of works as instructed by the WKCDA until the exceedance is abated. 		

 Table D-2:
 Event and Action Plan for Construction Noise

Landscape and Visual Impact

In case of non-compliance of landscape and visual impacts, procedures in accordance with the Event and Action Plan should be followed:

Event	Action					
	ET	IEC	WKCDA	Contractor		
Design Check	1. Design check to make sure the design complies with all the proposed mitigation measures in the EIA report;	 Check report submitted by ET; Recommend remedial design if necessary. 	1. Undertake remedial design if necessary.	-		
	2. Prepare and submit report.					
Non-conformity on one occasion	1. Identify source of non- conformity;	1. Check and verify source of non-conformity;	 Notify Contractor; Ensure remedial 	1. Amend working method as necessary;		
	2. Report to IEC and WKCDA;	2. Discuss remedial actions with ET and Contractor;	actions are properly implemented.	2. Rectify damage and undertake necessary		
	3. Discuss remedial actions with IEC, WKCDA and Contractor;			replacement and remedial actions.		
	4. Monitor remedial actions until rectification has been completed.					
Repeated non conformity	-1. Identify source of non- conformity;	1. Check and verify source of non-conformity;	 Notify Contractor; Ensure remedial actions are properly implemented. 	1. Amend working method as necessary;		
	 Report to IEC and WKCDA; Increase monitoring frequency; Discuss remedial actions with IEC, WKCDA and Contractor; 	2. Check Contractor's working method;		undertake necessary		
		3. Discuss remedial actions with ET and	replacement and remedial actions.			
		effectiveness of proposed				
	5. Monitor remedialremedial actions;actions until rectification5. Supervisehas been completed;implementation of					
	6. If non-conformity rectified, reduce monitoring frequency back to normal.	remedial actions.				

E. Monitoring Schedule

APRIL 2019

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1 AM1, AM2B - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring	2	3	4	5	6 AM1, AM2B - 24hrTSP, 1hr TSP x3
7	8	9	10	11 AM1, AM2B - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring		13
14	15	16	17 AM1, AM2B - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring		19	20
21	22	23 AM1, AM2B - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring		25	26	27
28	AM1, AM2B - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring					
		AM2B - Austin Road \	I ommerce Centre (ICC) West (Opposite to The Commerce Centre (ICC	Harbourside)	I	

MAY 2019

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			1	2	3 AM1, AM2B - 24hrTSP, 1hr TSP x3	4
5	6	7	8	9 AM1, AM2B - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring		11
12	13	14	15 AM1, AM2B - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring		17	18
19	20	21 AM1, AM2B - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring		23	24	25
26	AM1, AM2B - 24hrTSP, 1hr TSP x3 NM1A - Noise Impact Monitoring		29	30	31 AM1, AM2B - 24hrTSP, 1hr TSP x3	
		AM2B - Austin Road \	I ommerce Centre (ICC) West (Opposite to The Commerce Centre (ICC	Harbourside)	<u> </u>	

F. Calibration Certifications

29

High-Volume TSP Sampler 5-Point Calibration Record Location AM1(ICC) : Calibrated by K.T.Ho : : 04/02/2019 Sampler TE-5170 : Serial Number S/N 0767 :

Calibration Orifice and Standard	d Calibrat	ion Relationship
Serial Number	:	2454
Service Date	:	19 Mar 2018
Slope (m)	:	2.05242
Intercept (b)	:	-0.01383
Correlation Coefficient(r)	:	0.99994
Standard Condition		
Pstd (hpa)	:	1013
Tstd (K)	:	298.18
Calibration Condition		

Calibration Condition		
Pa (hpa)	:	1021
Ta(K)	:	295

Resi	stance Plate	dH [green liquid]	Z	X=Qstd	IC	Y
		(inch water)		(cubic meter/min)	(chart)	(corrected)
1	18 holes	11.2	3.377	1.652	58	58.52
2	13 holes	8.2	2.889	1.415	50	50.45
3	10 holes	6.2	2.512	1.231	42	42.38
4	7 holes	4.4	2.117	1.038	34	34.31
5	5 holes	2.6	1.627	0.799	22	22.20

8

Notes:Z=SQRT{dH(Pa/Pstd)(Tstd/Ta)}, X=Z/m-b, Y(Corrected Flow)=IC*{SQRT(Pa/Pstd)(Tstd/Ta)}

Sampler Calibration Relationship

Slope(m):42.659

Date

Model

Intercept(b):-10.770

Correlation Coefficient(r): 0.9971

Checked by:

Magnum Fan

Date: 07/02/2019



RECALIBRATION DUE DATE: March 19, 2019

nmental Certificate of Calibration

			Calibration	Certificati	on Informat	ion		
Cal. Date:	March 19,	2018	Roots	meter S/N:	438320 Ta: 294		294	°K
Operator:	Jim Tisch					Pa:	746.8	mm Hg
Calibration Model #: TE-5025A Cali			Calil	orator S/N:	2454	N		0
		Vol. Init	Vol. Final	ΔVol.	ΔTime	ΔΡ	ΔН]
	Run	(m3)	(m3)	(m3)	(min)	(mm Hg)	(in H2O)	
	1	1	2	1	1.4300	3.2	2.00	
	2	3	4	1	1.0040	6.4	4.00	1
	3	5	6	1	0.9030	7.9	5.00	
	4	7	8	1	0.8590	8.7	5.50	
	5	9	10	1	0.7080	12.8	8.00	
			E	Data Tabula	tion			ĺ
	Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right)}$)(<u>Tstd</u>)		Qa	$\sqrt{\Delta H(Ta/Pa)}$	
	(m3)	(x-axis)	(y-ax	is)	Va	(x-axis)	(y-axis)	
	0.9917	0.6935	1.41:	13	0.9957	0.6963	0.8874	
	0.9874	0.9835	1.995	59	0.9914	0.9875	1.2549	
	0.9854	1.0913	2.233	15	0.9894	1.0957	1.4030	
	0.9843	1.1459	2.340	05	0.9883	1.1506	1.4715	
	0.9789	1.3826	2.822	27	0.9829	1.3882	1.7747	
		m=	2.052	42		m=	1.28519	
	QSTD	b=	-0.013		QA	b=	-0.00869	
	L	r=	0.999	94		r=	0.99994	
				Calculatio	ns			
			/Pstd)(Tstd/Ta	a)	Va=	∆Vol((Pa-∆I	P)/Pa)	
	Qstd=	Vstd/∆Time			Qa=	Va/∆Time		
	For subsequent fl			ent flow ra	te calculation	15:		
	Qstd= $1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b$))-b)	Qa=	1/m ((√∆⊦	I(Ta/Pa))-b)	
		Conditions	1					
Tstd:						RECA	LIBRATION	
Pstd:	1	mm Hg (ey			US FPA reco		nual recalibratio	n nor 1000
AH: calibrat		er reading (i	n H2O)				Regulations Part 5	
		eter reading					Reference Meth	10 50
		perature (°K)						
		essure (mm	Hg)				ended Particulate	
b: intercept				the	e Atmosphe	re, 9.2.17, page 3	30	

Tisch Environmental, Inc. 145 South Miami Avenue Village of Cleves, OH 45002

b: intercept m: slope

	High-Volume TSP Sampler		
	5-Point Calibration Record		
Location	:	AM1(ICC)	
Calibrated by	:	K.T.Ho	
Date	:	04/04/2019	
<u>Sampler</u>			
Model	:	TE-5170	
Serial Number	:	S/N 0767	

Calibration Orifice and Standard Calibration Relationship					
Serial Number	:	2454			
Service Date	:	25 February 2019			
Slope (m)	:	2.07076			
Intercept (b)	:	-0.02917			
Correlation Coefficient(r)	:	1.00000			

Standard Condition		
Pstd (hpa)	:	1013
Tstd (K)	:	298.18
Calibration Condition		
Pa (hpa)	:	1010
Ta(K)	:	301

Resi	istance Plate	dH [green liquid]	Z	X=Qstd	IC	Y
		(inch water)		(cubic meter/min)	(chart)	(corrected)
1	18 holes	12.0	3.442	1.676	60	59.61
2	13 holes	8.2	2.845	1.388	52	51.66
3	10 holes	6.2	2.474	1.209	42	41.73
4	7 holes	3.8	1.937	0.949	32	31.79
5	5 holes	2.2	1.474	0.726	20	19.87

Notes:Z=SQRT{dH(Pa/Pstd)(Tstd/Ta)}, X=Z/m-b, Y(Corrected Flow)=IC*{SQRT(Pa/Pstd)(Tstd/Ta)}

Sampler Calibration Relationship

Slope(m):<u>42.230</u>

Intercept(b): <u>-9.303</u>

Correlation Coefficient(r): 0.9938

Checked by:

Magnum Fan

Date: 06/04/2019

High-Volume TSP Sampler 5-Point Calibration Record

Location	:	AM2B (The Harbourside)
Calibrated by	:	K.T.Ho
Date	:	20/03/2019
<u>Sampler</u> Model Serial Number	:	TE-5170 S/N 8919

Calibration Orifice and Standard	d Calibra	tion Relationship
Serial Number	:	2454
Service Date	:	25 February 2019
Slope (m)	:	2.07076
Intercept (b)	:	-0.02917
Correlation Coefficient(r)	:	1.00000
Slope (m) Intercept (b)	:	2.07076 -0.02917

Standard Condition		
Pstd (hpa)	:	1013
Tstd (K)	:	298.18
Calibration Condition		
Pa (hpa)	:	1018
Ta(K)	:	296

Resi	stance Plate	dH [green liquid]	Z	X=Qstd	IC	Y
		(inch water)		(cubic meter/min)	(chart)	(corrected)
1	18 holes	12.0	3.484	1.704	58	58.34
2	13 holes	9.0	3.018	1.477	52	52.30
3	10 holes	6.2	2.505	1.227	42	42.25
4	7 holes	4.0	2.012	0.987	34	34.20
5	5 holes	2.0	1.422	0.700	22	22.13

Notes:Z=SQRT{dH(Pa/Pstd)(Tstd/Ta)}, X=Z/m-b, Y(Corrected Flow)=IC*{SQRT(Pa/Pstd)(Tstd/Ta)}

Sampler Calibration Relationship

Slope(m):<u>36.311</u> Intercept(b):-2.421

Correlation Coefficient(r): 0.9977

Checked by:

Magnum Fan

1

Date: 22/03/2019

1S nviro				J)			CALIBRATION DUE DATE: Jary 25, 202
		tifu	cate	/			ntion	
C-1 D-1			Calibration					
	February 25 lim Tisch	, 2019	Roots	meter S/N:	438320		294 762.0	°K
Calibration N		TE-5025A	Cali	brator S/N:	2454	Pa:	762.0	mm Hg
	1040111							
	Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)	
	1	1	2	(m3)	1.4400	(mm ng) 3.2	2.00	
	2	3	4	1	1.0200	6.4	4.00	
	3	5	6	1	0.9120	7.9	5.00 5.50	
	5	9	10	1	0.7180	12.8	8.00	
Í			8	Data Tabula	tion			
	Vstd	Qstd	√∆H(<u>Pa</u> Pstc	$T \left(\frac{1310}{Ta} \right)$		Qa	√∆H(Ta/Pa)	
	(m3)	(x-axis)	(y-a)		Va	(x-axis)	(y-axis)	
	1.0120	0.7028	1.42		0.9958	0.6915	0.8784	
	1.0057	1.1028	2.25	42	0.9896	1.0851	1.3889	
	1.0045	1.1546	2.36		0.9885	1.1362 1.3694	1.4567 1.7569	
	0.9992	1.5910 m=	2.05		0.9632	1.5094 m=	1.29667	
	QSTD	b=	-0.02		QA	b=	-0.01797	
		r=	1.000	000		r=	1.00000	
			10-+-11/2-+-1/2	Calculatio			2) /0-)	
		ΔVol((Pa-ΔP) Vstd/ΔTime	/Pstd)(Tstd/T	aj		ΔVol((Pa-Δl Va/ΔTime	-//Pa)	
			For subsequ	uent flow ra	te calculatio			
	Qstd=	1/m ((_AH(Pa Pstd / Tstd Ta		Qa=	1/m ((√∆H	l(Ta/Pa))-b)	
		Conditions]				
Tstd: Pstd:	298.15 760	°K mm Hg			-	RECA	LIBRATION	
	ŀ	ley	110.61		10000000000000000000000000000000000000		nnual recalibratio	
ΔH: calibrato	ter manomet	er reading (i eter reading	(mm Hg)		and the second second second		Regulations Part , Reference Meth	and the second
Ta: actual ab	solute tem	perature (°K)					ended Particulat	
Par actual ba	rometric pr	ressure (mm	Hg)		th	e Atmosphe	ere, 9.2.17, page	30
b: intercept								

SIBATA

SIBATA SCIENTIFIC TECHNOLOGY LTD.

1-1-62, Nakane, Soka, Saitama, 340-0005 Japan TEL: 048-933-1582 FAX: 048-933-1591

CALIBRATION CERTIFICATE

Date: April 6th, 2018

Equipment Name	: Digital Dust Indicator, Model LD-5R
Code No.	: 080000-72
Quantity	: 1 unit
Serial No.	: 841723
Sensitivity	: 0.001 mg/m3
Sensitivity Adjustment	: 615CPM
Scale Setting	: April 2rd, 2018

We hereby certify that the avobe mentioned instrment has been calibrated satisfactory.

Sincerely

SIBATA SCIENTIFIC TECHNOLOGY LTD.

ling Theney

Tong Zhang Overseas Sales Division



REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

PROJECT NAME	: HK180419 : PERFORMANCE CHECK / CALIBRATION OF DUST METER : 2/5/2018				
	: Envirotech Services Company : Rm. 113, 1/F., MY LOFT, 9 HOI WING ROAD, TUEN MUN, N.T.				
REPORT NO.	: HK180419				
PROJECT ITEM NO.	: HK180419-01				
PERFORMANCE CHECK / CALIBRATED EQUIPM	IENT				
TYPE	: Digital Dust Indicator				
MANUFACTURER	: SIBATA				
MODEL NO.	: LD-5R				
SERIAL NO.	: 841723				
EQUIPMENT NO.					
RECEIPT DATE	: 27/4/2018				
PERFORMANCE CHECK / CALIBRATION DATE : 28/4/2018					

PERFORMANCE CHECK / CALIBRATION Information

CODE	Calibration Parameter	Method Procedure	Reference Method
Dust PC/CAL	Performance Check / Calibration of Dust Meter	CAL003	General Technical Requirements of Environmental Monitoring, Environmental Monitoring & Audit Guidelines for Development Projects in HK

 Notes :
 1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.

 2.
 Performance Check / Calibration result relates to performance check / calibration item(s) as received.

Approved Signatory

:

Wong Po Yan Pauline (Assistant Laboratory Manager)

Issue Date:

2/5/2018



REPORT OF PERFORMANCE CHECK / CALIBRATION PROJECT NAME DATE OF ISSUE PERFORMANCE CHECK / CALIBRATION OF DUST METER 2/5/2018 REPORT NO. HK180419 PERFORMANCE CHECK / CALIBRATED EQUIPMENT TYPE Digital Dust Indicator MANUFACTURER SIBATA MODEL NO. LD-5R SERIAL NO. EQUIPMENT NO. SENSITIVITY ADJUSTMENT (CPM) 841723 615 PERFORMANCE CHECK / CALIBRATION DATE 28/4/2018 STANDARD EQUIPMENT HIGH VOLUME AIR SAMPLER TISCH MANUFACTURER MODEL NO. TE-5170 EQUIPMENT REF NO. PTL_HV002 LAST CALIBRATION DATE 27/4/2018


EQUIPMENT PERFORMANCE CHECK / CALIBRATION RESULTS:

Sensitivity Adjustment Scale Setting (Before Performance check / Calibration): 615 Sensitivity Adjustment Scale Setting (After Performance check / Calibration): 615

		Mean Temp (°C)		Concentration in ug/m ³	Total	Concentration in Count/Minute ³
Trial no. in 1-hr period	Time		Mean Pressure (hPa)	(Standard equipment)	Count ²	(Performance Check / Calibrated equipment)
				(Y - Axis)	(Performance Check / Calibrated equipment)	(X - Axis)
Zero Check ¹	28/4/2018,9:50:00 AM	24.9	1015	- 0	0	0
1	28/4/2018,11:32:00 AM	24.9	1015	53	3926	65
2	28/4/2018,12:38:00 PM	24.9	1015	58	4121	69
3	28/4/2018,1:46:00 PM	24.9	1015	16	618	10

CPM

CPM



Notes: 1.

1. Zero check conducted as per CAL003 SOP and manufacturer's manual as appropriate.

- 2. Total Count was measured by Digital Dust Indicator.
- 3. Count/minute was calcuated by (Total Count/60)

4. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.

5. Performance Check / Calibration result relates to performance check / calibration item(s) as received.

Operator:	MA Ching Him, Jackey	Signature:	397	Date:	28/4/2018
Checked by:	Wong Po Yan, Pauline	Signature:	prif	Date:	2/5/2018



SIBATA SCIENTIFIC TECHNOLOGY LTD.

1-1-62, Nakane, Soka, Saitama, 340-0005 Japan TEL: 048-933-1582 FAX: 048-933-1591

CALIBRATION CERTIFICATE

Date: April 6th, 2018

Equipment Name	:	Digital Dust Indicator, Model LD-5R
Code No.	:	080000-72
Quantity		1 unit
Serial No.	:	841724
Sensitivity	:	0.001 mg/m3
Sensitivity Adjustment	:	618CPM
Scale Setting	:	April 2rd, 2018

We hereby certify that the avobe mentioned instrment has been calibrated satisfactory.

Sincerely

SIBATA SCIENTIFIC TECHNOLOGY LTD.

long Zhang

Tong Zhang Overseas Sales Division

PILOT

REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

REPORT NO. PROJECT NAME DATE OF ISSUE	: HK180420 : PERFORMANCE CHECK / CALIBRATION OF DUST METER : 2/5/2018	
CUSTOMER	: Envirotech Services Company	
ADDRESS	: Rm. 113, 1/F., MY LOFT, 9 HOI WING ROAD, TUEN MUN, N.T.	
REPORT NO.	: HK180420	
PROJECT ITEM NO.	: HK180420-01	
PERFORMANCE CHECK / CALIBRATED	EQUIPMENT	
TYPE	: Digital Dust Indicator	
MANUFACTURER	: SIBATA	
MODEL NO.	: LD-5R	
SERIAL NO.	: 841724	
EQUIPMENT NO.		
RECEIPT DATE	: 27/4/2018	
PERFORMANCE CHECK / CALIBRATION	I DATE : 28/4/2018	

PERFORMANCE CHECK / CALIBRATION Information

CODE	Calibration Parameter	Method Procedure	Reference Method
Dust PC/CAL	Performance Check / Calibration of Dust Meter	CAL003	General Technical Requirements of Environmental Monitoring, Environmental Monitoring & Audit Guidelines for Development Projects in HK

 Notes : 1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.

 2. Performance Check / Calibration result relates to performance check / calibration item(s) as received.

Approved Signatory

Wong Po Yan Pauline

(Assistant Laboratory Manager)

Issue Date:

2/5/2018



REPORT OF PERFORMANCE CHECK / CALIBRAT PROJECT NAME DATE OF ISSUE REPORT NO.	TION : PERFORMANCE CHECK / CALIBRATION OF DUST METER : 2/5/2018 : HK180420
PERFORMANCE CHECK / CALIBRATED EQUIPME	ENT
TYPE	: Digital Dust Indicator
MANUFACTURER	: SIBATA
MODEL NO.	: LD-5R
SERIAL NO.	: 841724
EQUIPMENT NO.	
SENSITIVITY ADJUSTMENT (CPM)	: 618
PERFORMANCE CHECK / CALIBRATION DATE	: 28/4/2018
STANDARD EQUIPMENT	
TYPE	HIGH VOLUME AIR SAMPLER
MANUFACTURER	: TISCH
MODEL NO.	: TE-5170
EQUIPMENT REF NO.	: PTL HV002
LAST CALIBRATION DATE	: 27/4/2018

EQUIPMENT PERFORMANCE CHECK / CALIBRATION RESULTS:

Sensitivity Adjustment Scale Setting (Before Performance check / Calibration): Sensitivity Adjustment Scale Setting (After Performance check / Calibration):


Trial no. in 1-hr period			Mean Pressure (hPa)	Concentration in ug/m ³	Total	Concentration in Count/Minute ³
	Time	Mean Temp (°C)		(Standard equipment)	Count ²	(Performance Check / Calibrated equipment)
				(Y - Axis)	(Performance Check / Calibrated equipment)	(X - Axis)
Zero Check ¹	28/4/2018,9:50:00 AM	24.9	1015	- 0	0	0
1	28/4/2018,11:32:00 AM	24.9	1015	53	3840	64
2	28/4/2018,12:38:00 PM	24.9	1015	58	4079	68
3	28/4/2018,1:46:00 PM	24.9	1015	16	604	10


617

617

CPM

СРМ





Notes: 1.

- Zero check conducted as per CAL003 SOP and manufacturer's manual as appropriate.
- 2. Total Count was measured by Digital Dust Indicator.
- 3. Count/minute was calcuated by (Total Count/60)
- 4. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
- 5. Performance Check / Calibration result relates to performance check / calibration item(s) as received.

Operator:	MA Ching Him, Jackey	Signature:	398	Date:	28/4/2018	
Checked by:	Wong Po Yan, Pauline	Signature:	DMtg	Date:	2/5/2018	



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書


Certificate No.: C183087 證書編號

ITEM TESTED / 送檢口 Description / 儀器名稱 Manufacturer / 製造商 Model No. / 型號 Serial No. / 編號 Supplied By / 委託者	 [頁目 (Job No. / 序引編號: IC18-1089) Sound Level Meter Rion NL-52 00175561 Envirotech Services Co. Room 113, 1/F, My Loft, 9 Hoi Wing New Territories, Hong Kong 	Date of Receipt / 收件日期: g Road, Tuen Mun,	25 May 2018
TEST CONDITIONS / Temperature / 溫度 : Line Voltage / 電壓 :		Relative Humidity / 相對濕度 :	(50 ± 25)%
TEST SPECIFICATIO Calibration check	NS / 測試規範		
DATE OF TEST / 測試	日期 : 10 June 2018		
The results do not exceed The results are detailed in The test equipment used	particular unit-under-test only. I manufacturer's specification. In the subsequent page(s). for calibration are traceable to National St ie Hong Kong Special Administrative Regi Keysight Technologies oratory, Germany	andards via : on Standard & Calibration Laboratory	
Tested By : 測試	K C Lee Engineer		
Certified By : 核證	<u>Chan Un Chan</u> H C Chan Engineer	Date of Issue : 14 June 2 簽發日期	2018

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

de.



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C183087 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration was performed before the test.
- 3. The results presented are the mean of 3 measurements at each calibration point.
- 4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C180024
CL281	Multifunction Acoustic Calibrator	PA160023

- 5. Test procedure : MA101N.
- 6. Results :
- 6.1 Sound Pressure Level
- 6.1.1 Reference Sound Pressure Level

UUT Setting			Applie	d Value	UUT	IEC 61672	
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _A	A	Fast	94.00	1	94.0	± 1.1

6.1.2 Linearity

	UU	T Setting	Applie	d Value	UUT		
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	
30 - 130	L _A	A	Fast	94.00	1	94.0 (Ref.)	
				104.00	[104.0	
				114.00] [114.0	

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting			Applied Value		UUT	IEC 61672	
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _A	A	Fast	94.00	1	94.0	Ref.
			Slow			94.0	± 0.3

2

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C183087 證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting			Applied Value		UUT	IEC 61672	
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _A	A	Fast	94.00	63 Hz	67.7	-26.2 ± 1.5
					125 Hz	77.8	-16.1 ± 1.5
					250 Hz	85.3	-8.6 ± 1.4
					500 Hz	90.8	-3.2 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	95.2	$+1.2 \pm 1.6$
					4 kHz	95.0	$+1.0 \pm 1.6$
					8 kHz	93.0	-1.1 (+2.1; -3.1
					12.5 kHz	89.6	-4.3 (+3.0 ; -6.0

6.3.2 C-Weighting

	UUT	Setting		Applied Value		UUT	IEC 61672 -
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _C	C	Fast	94.00	63 Hz	93.2	-0.8 ± 1.5
					125 Hz	93.8	-0.2 ± 1.5
					250 Hz	94.0	0.0 ± 1.4
					500 Hz	94.0	0.0 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	93.8	-0.2 ± 1.6
					4 kHz	93.2	-0.8 ± 1.6
					8 kHz	_ 91.1	-3.0 (+2.1;-3.1)
					12.5 kHz	87.6	-6.2(+3.0;-6.0)

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 10990

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :	94 dB : 63 Hz - 125 Hz 250 Hz - 500 Hz 1 kHz 2 kHz - 4 kHz 8 kHz 12.5 kHz 104 dB : 1 kHz	: $\pm 0.35 \text{ dB}$: $\pm 0.30 \text{ dB}$: $\pm 0.20 \text{ dB}$: $\pm 0.35 \text{ dB}$: $\pm 0.45 \text{ dB}$: $\pm 0.47 \text{ dB}$: $\pm 0.70 \text{ dB}$: $\pm 0.10 \text{ dB}$ (Ref. 94 dB)
	104 dB : 1 kHz 114 dB : 1 kHz	$\pm 0.10 \text{ dB} (\text{Ref. 94 dB})$ $\pm 0.10 \text{ dB} (\text{Ref. 94 dB})$

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C185607 證書編號

Description / 儀器名 Manufacturer / 製造j Model No. / 型號 Serial No. / 編號 Supplied By / 委託者	新 : LARSON DAVIS : CAL200 : 15678
TEST CONDITION Temperature / 溫度 Line Voltage / 電壓	: (23 ± 2)°C - Relative Humidity / 相對濕度 : (50 ± 25)%
TEST SPECIFICA Calibration check	TONS / 測試規範
The results do not exce The results are detailed The test equipment use - The Government of T - The Bruel & Kjaer C	particular unit-under-test only. ed manufacturer's specification. in the subsequent page(s). I for calibration are traceable to National Standards via : he Hong Kong Special Administrative Region Standard & Calibration Laboratory llibration Laboratory, Denmark / Keysight Technologies boratory, Germany
The results apply to the The results do not exce The results are detailed The test equipment use - The Government of T - The Bruel & Kjaer C - Agilent Technologies - Rohde & Schwarz La	particular unit-under-test only. ed manufacturer's specification. in the subsequent page(s). I for calibration are traceable to National Standards via : he Hong Kong Special Administrative Region Standard & Calibration Laboratory llibration Laboratory, Denmark / Keysight Technologies boratory, Germany

written approval of this laboratory. 本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 — 校正及檢測實驗所 c/o 香港新界屯門興安里一號四樓 Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: cr

E-mail/電郵: callab@suncreation.com Website/網址

Website/網址: www.suncreation.com



Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C185607 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- 2. The results presented are the mean of 3 measurements at each calibration point.
- 3. Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C183775
CL281	Multifunction Acoustic Calibrator	CDK1806821
TST150A	Measuring Amplifier	C181288

- 4. Test procedure : MA100N.
- 5. Results :
- 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)		
94 dB, 1 kHz	94.0	± 0.2	± 0.2		
114 dB, 1 kHz	113.9				

5.2 Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value		
(kHz)	(kHz)	Spec.	(Hz)		
1	1.000	1 kHz ± 1 %	± 1		

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.


The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

G. Graphical Plots of the Monitoring Results

				Conc. (μg/m³)			Action	Limit	
	Weather				_			Level	Level
Date	Condition	T	Time		1 st Hour	2 nd Hour	3 rd Hour	(µg/m³)	(µg/m³)
1-Apr-19	Cloudy	8:00	-	11:00	42	39	45	273.7	500
6-Apr-19	Sunny	8:02	-	11:02	64	61	60	273.7	500
11-Apr-19	Fine	7:50	-	10:50	74	69	79	273.7	500
17-Apr-19	Cloudy	7:52	-	10:52	41	38	32	273.7	500
23-Apr-19	Fine	7:53	-	10:53	41	38	44	273.7	500
29-Apr-19	Fine	7:52	-	10:52	41	39	33	273.7	500


Air Quality Monitoring Result at Station AM1 (1-hour TSP)

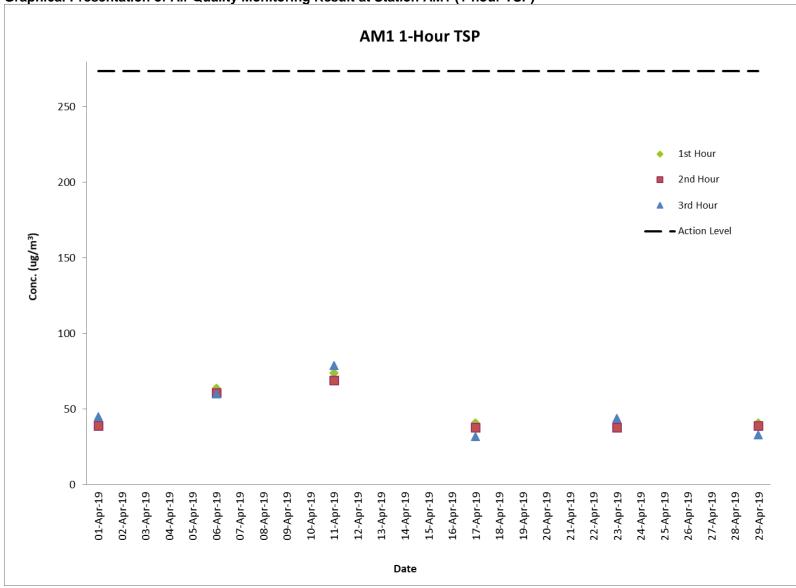

Graphical Presentation of Air Quality Monitoring Result at Station AM1 (1-hour TSP)

						Conc. (µg/m ³)	Action	Limit
	Weather							Level	Level
Date	Condition		Tim	ie	1 st Hour	2 nd Hour	3 rd Hour	(µg/m³)	(µg/m³)
1-Apr-19	Cloudy	8:17	-	11:17	49	47	44	274.2	500
6-Apr-19	Sunny	8:16	-	11:16	71	68	69	274.2	500
11-Apr-19	Fine	8:07	-	11:07	91	97	94	274.2	500
17-Apr-19	Cloudy	8:07	-	11:07	45	52	50	274.2	500
23-Apr-19	Fine	8:07	-	11:07	49	54	55	274.2	500
29-Apr-19	Fine	8:07	-	11:07	44	49	52	274.2	500


Air Quality Monitoring Result at Station AM2B (1-hour TSP)

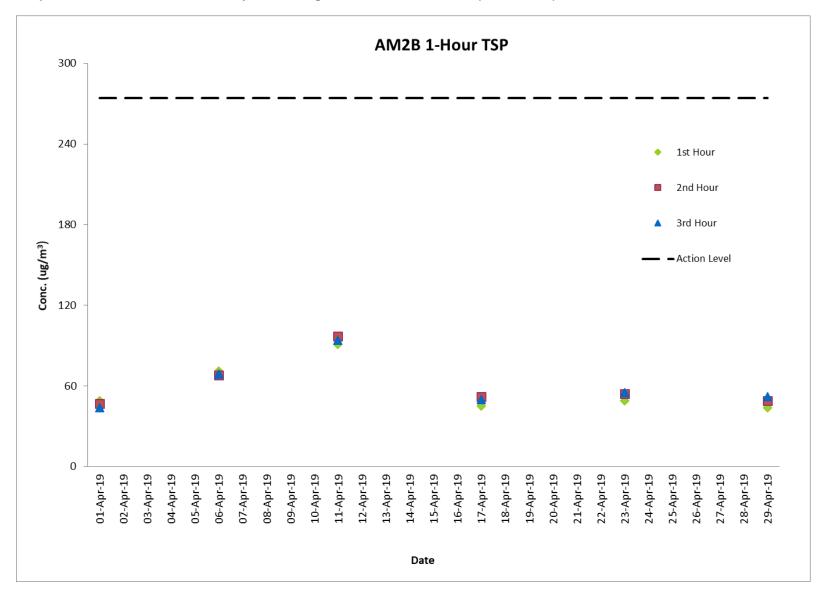

Graphical Presentation of Air Quality Monitoring Result at Station AM2B (1-hour TSP)

Star	't	Finis	sh	Filter W	eight (g)		d Time ding	Sampling Flow Rate (m ³ /min)		Conc.	Weather	Action	Limit		
Date	Time	Date	Time	Initial	Final	Initial	Final	Time (hrs)	Initial	Final	Average	(µg/m ³)	Condition	Level	Level
1-Apr-19	8:02	2-Apr-19	8:02	2.637	2.7135	24024.38	24048.38	24	1.24	1.24	1.24	43	Cloudy	143.6	260
6-Apr-19	8:00	7-Apr-19	8:00	2.6376	2.7167	24048.38	24072.38	24	1.24	1.24	1.24	44	Sunny	143.6	260
11-Apr-19	7:52	12-Apr-19	7:52	2.6228	2.735	24072.38	24096.38	24	1.24	1.24	1.24	63	Fine	143.6	260
17-Apr-19	7:50	18-Apr-19	7:50	2.6411	2.7332	24096.38	24120.38	24	1.24	1.24	1.24	52	Cloudy	143.6	260
23-Apr-19	10:20	24-Apr-19	10:20	2.6705	2.7397	24120.38	24144.38	24	1.24	1.24	1.24	39	Fine	143.6	260
29-Apr-19	7:50	30-Apr-19	7:50	2.7111	2.7592	24144.38	24168.38	24	1.24	1.24	1.24	27	Fine	143.6	260


Air Quality Monitoring Result at Station AM1 (24-hour TSP)

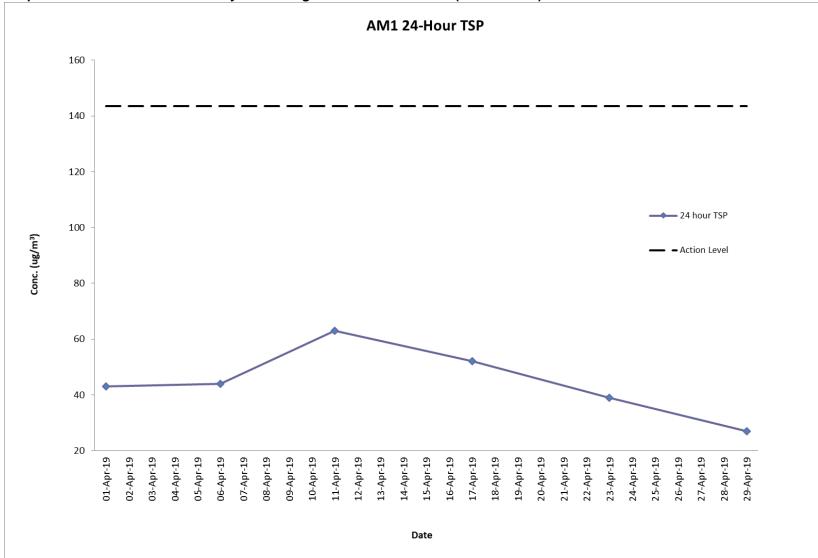

Graphical Presentation of Air Quality Monitoring Result at Station AM1 (24-hour TSP)

Star	rt	Finis	sh	Filter W	eight (g)		d Time ding	Sampling	Flow	Rate (m ³ /	min)	Conc.	Weather	Action	Limit
Date	Time	Date	Time	Initial	Final	Initial	Final	Time (hrs)	Initial	Final	Average	(µg/m ³)	Condition	Level	Level
1-Apr-19	8:15	2-Apr-19	8:15	2.6444	2.7520	19679.05	19703.05	24	1.17	1.17	1.17	64	Cloudy	151.1	260
6-Apr-19	8:14	7-Apr-19	8:14	2.6298	2.7248	19703.05	19727.05	24	1.17	1.17	1.17	56	Sunny	151.1	260
11-Apr-19	8:05	12-Apr-19	8:05	2.6124	2.7474	19727.05	19751.05	24	1.17	1.17	1.17	80	Fine	151.1	260
17-Apr-19	8:05	18-Apr-19	8:05	2.7039	2.8092	19751.05	19775.05	24	1.17	1.17	1.17	63	Cloudy	151.1	260
23-Apr-19	8:05	24-Apr-19	8:05	2.7053	2.7848	19775.05	19799.05	24	1.17	1.17	1.17	47	Fine	151.1	260
29-Apr-19	8:05	30-Apr-19	8:05	2.6970	2.7852	19799.05	19823.05	24	1.17	1.17	1.17	52	Fine	151.1	260

Air Quality Monitoring Result at Station AM2B (24-hour TSP)

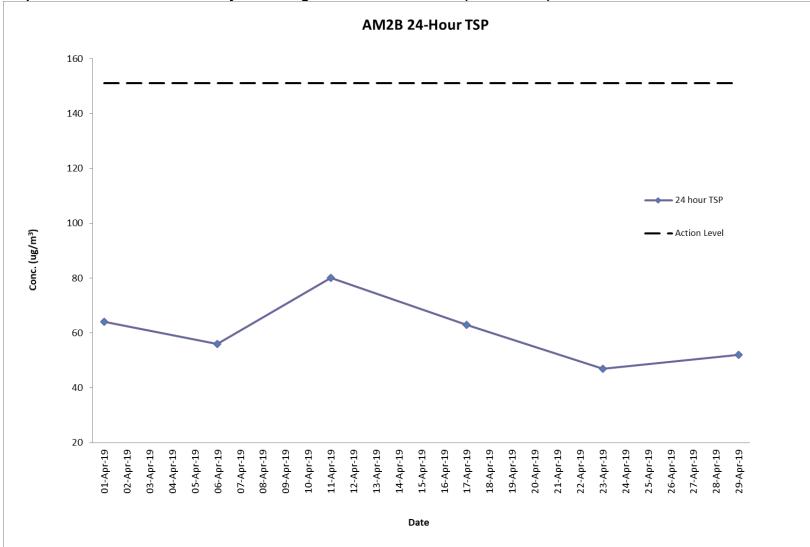

Graphical Presentation of Air Quality Monitoring Result at Station AM2B (24-hour TSP)

Date	Time	Measured L ₁₀ , dB(A)	Measured L ₉₀ , dB(A)	L _{eq} (30 min.)*, dB(A)
1-Apr-19	10:24	68.6	64.1	
1-Apr-19	10:29	66.4	62.0	
1-Apr-19	10:34	67.5	63.3	<u> </u>
1-Apr-19	10:39	68.3	64.1	69
1-Apr-19	10:44	66.1	62.7	
1-Apr-19	10:49	67.5	63.3	
11-Apr-19	10:14	66.5	62.3	
11-Apr-19	10:19	67.4	63.1	
11-Apr-19	10:24	66.6	62.5	<u> </u>
11-Apr-19	10:29	67.3	63.4	68
11-Apr-19	10:34	66.7	62.6	
11-Apr-19	10:39	66.5	62.3	
17-Apr-19	10:14	67.8	63.7	
17-Apr-19	10:19	68.6	64.2	
17-Apr-19	10:24	69.5	65.6	60
17-Apr-19	10:29	67.9	63.5	69
17-Apr-19	10:34	66.2	62.6	
17-Apr-19	10:39	67.3	63.3	
23-Apr-19	10:10	66.0	62.7	
23-Apr-19	10:15	68.3	64.1	
23-Apr-19	10:20	68.9	64.5	69
23-Apr-19	10:25	67.6	63.2	68
23-Apr-19	10:30	66.4	63.0	
23-Apr-19	10:35	66.5	62.5	
29-Apr-19	10:12	66.4	62.2	
29-Apr-19	10:17	67.9	63.5	
29-Apr-19	10:22	68.0	64.1	60
29-Apr-19	10:27	69.3	65.5	69
29-Apr-19	10:32	66.5	62.3	
29-Apr-19	10:37	67.7	63.4	


Noise Monitoring Result at Station NM1A

Remarks:

* +3dB (A) correction was applied to free-field measurement.




The station set-up of a free-field measurement at Station NM1A.

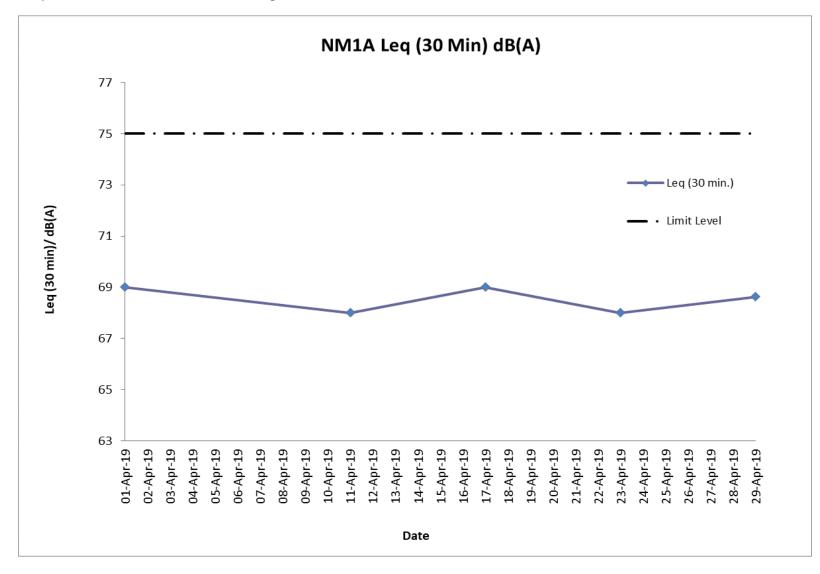


Graphical Presentation Noise Monitoring Result at Station NM1A


H. Meteorological Data Extracted from Hong Kong Observatory

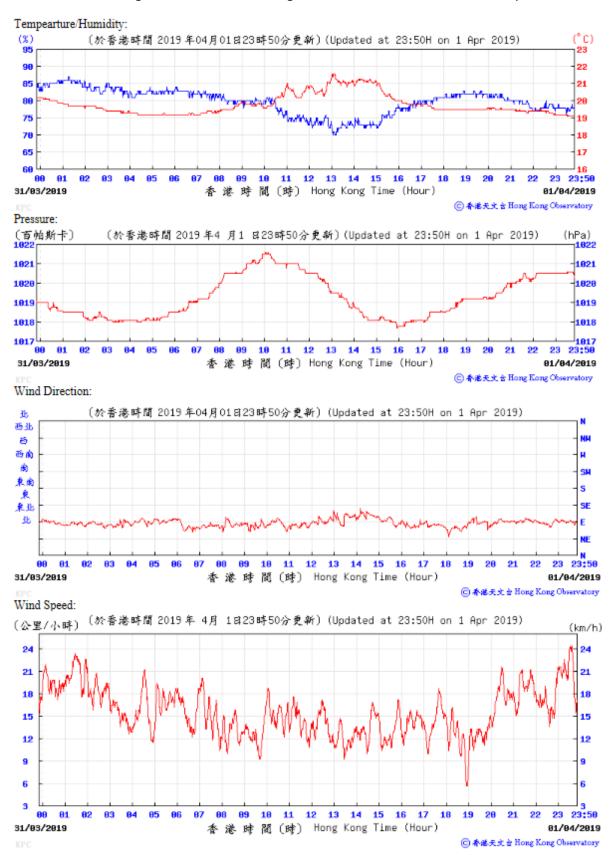



Extract of Meteorological Observations for King's Park Automatic Weather Station, April 2019

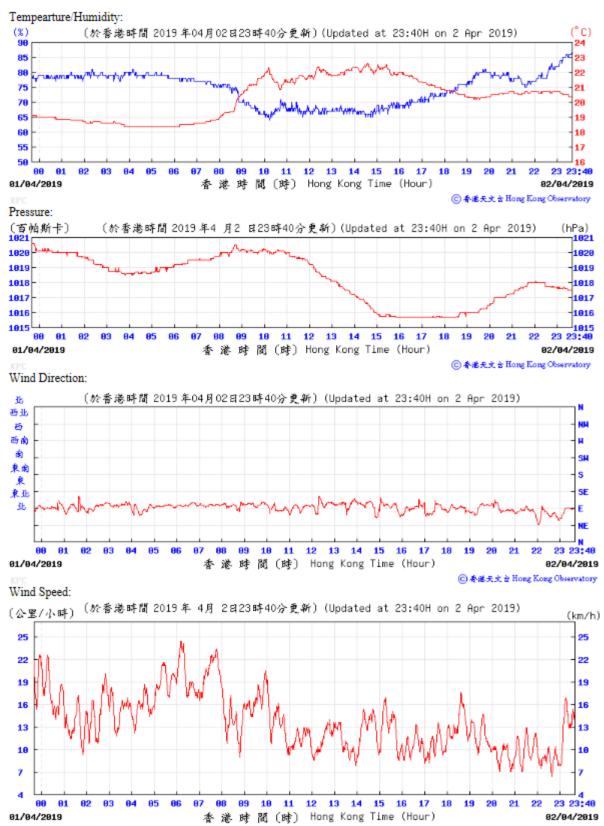



ⓒ 養護天文 술 Hong Kong Observatory

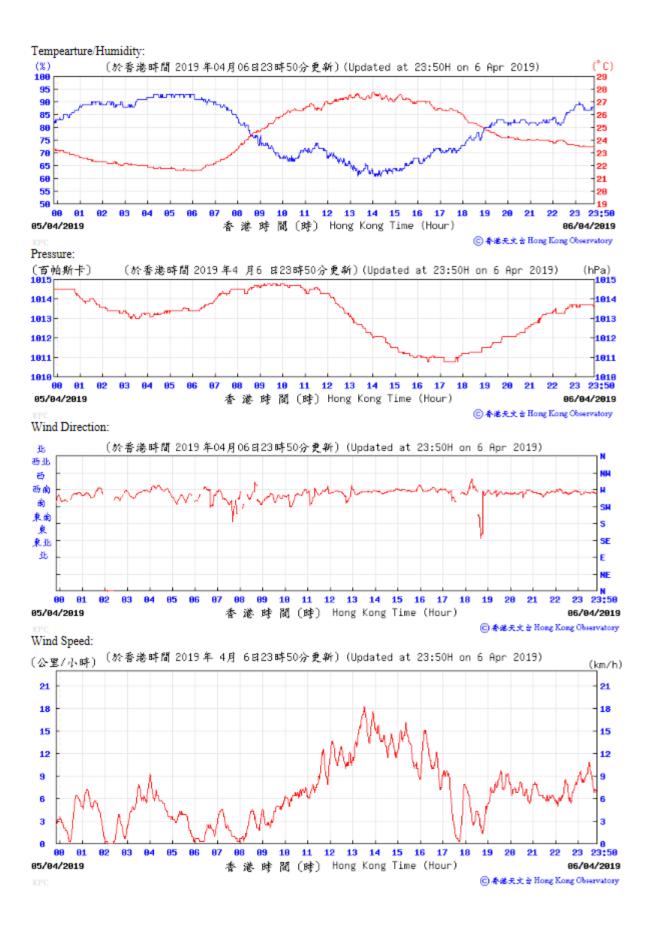


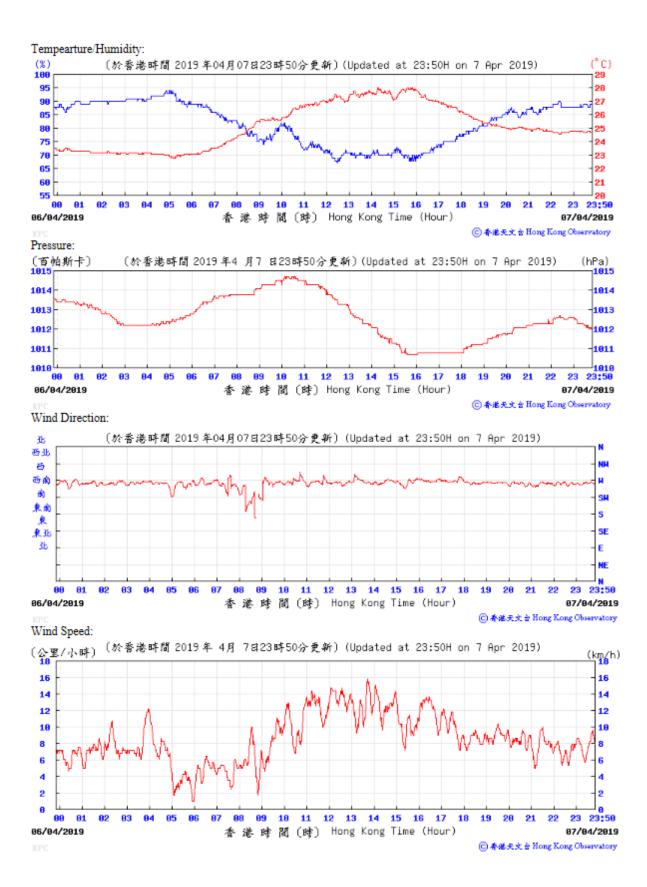


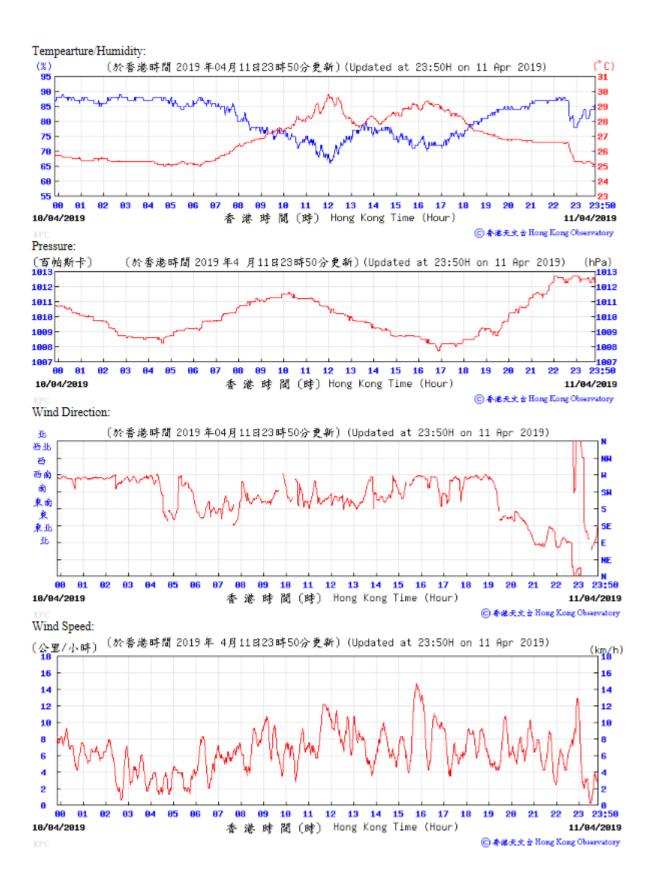


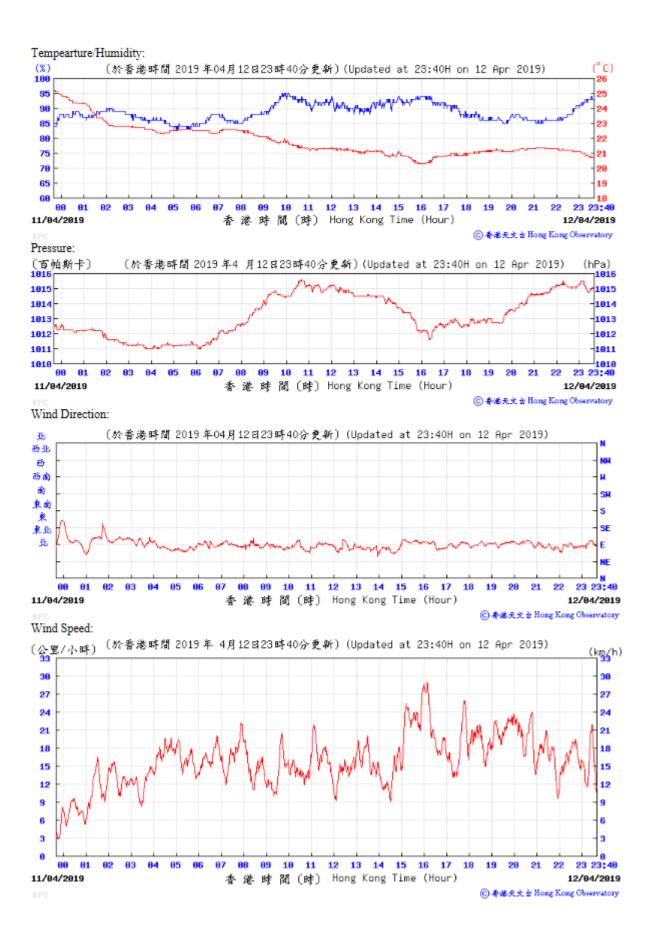


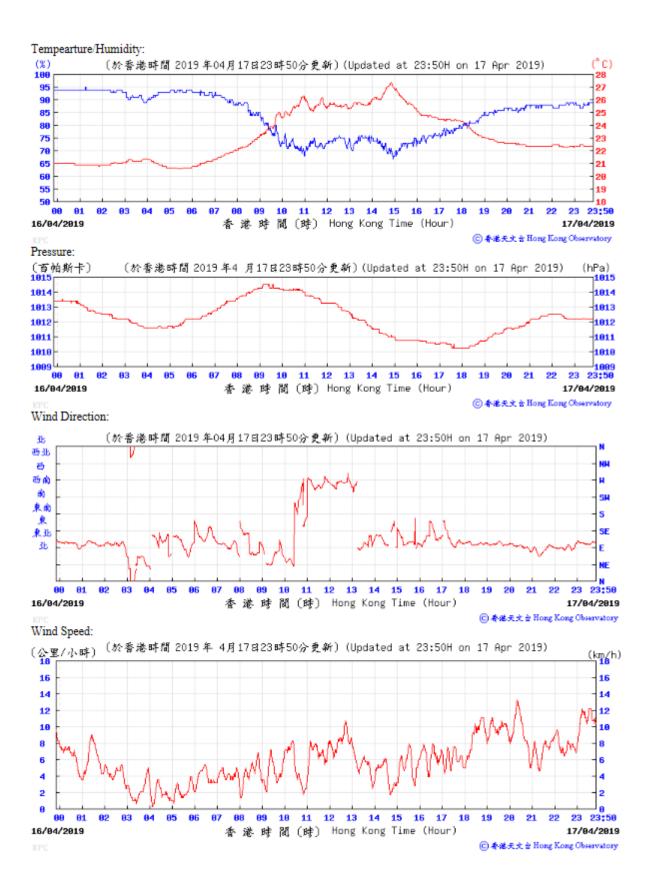


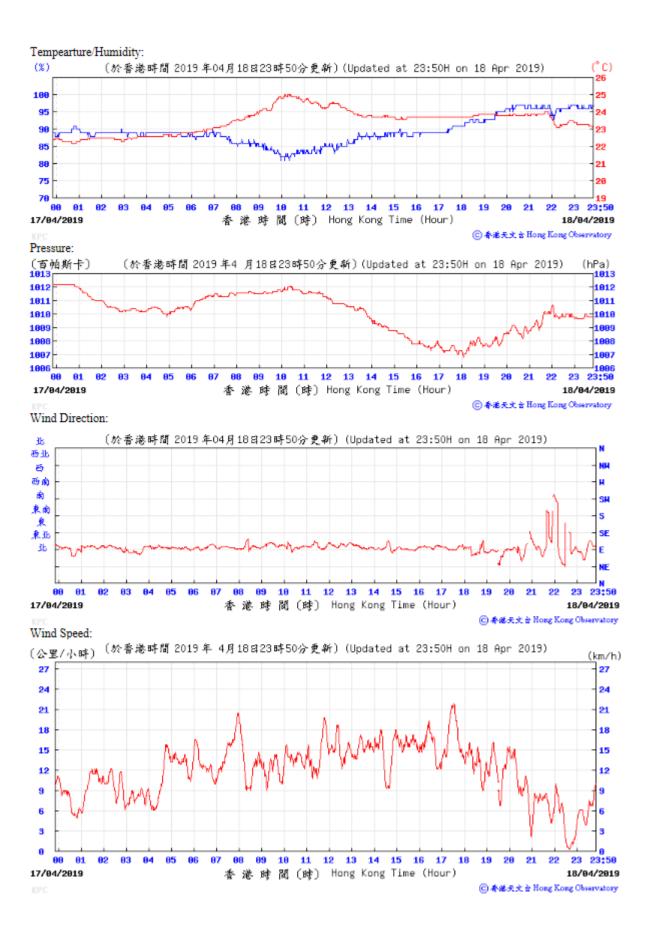

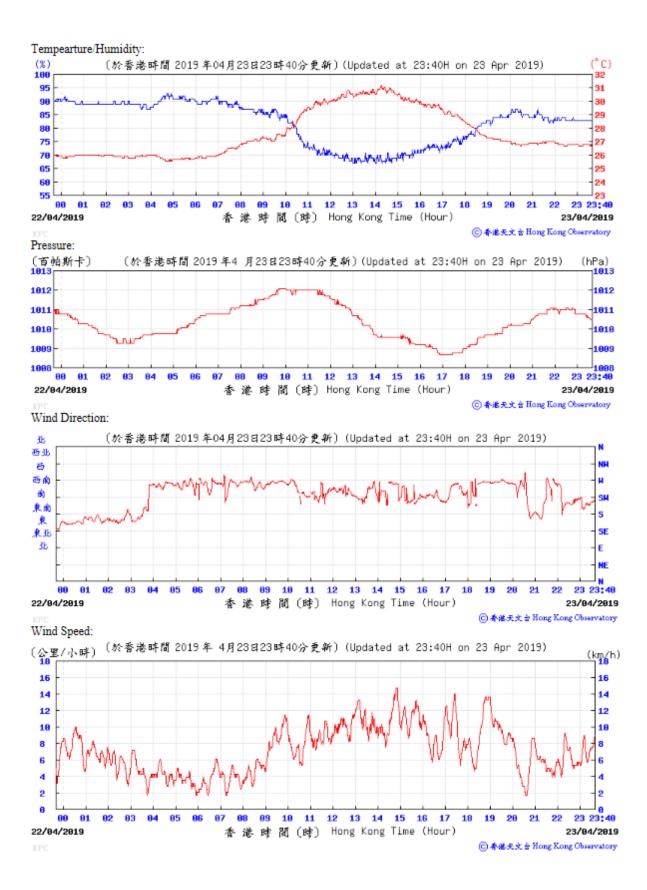

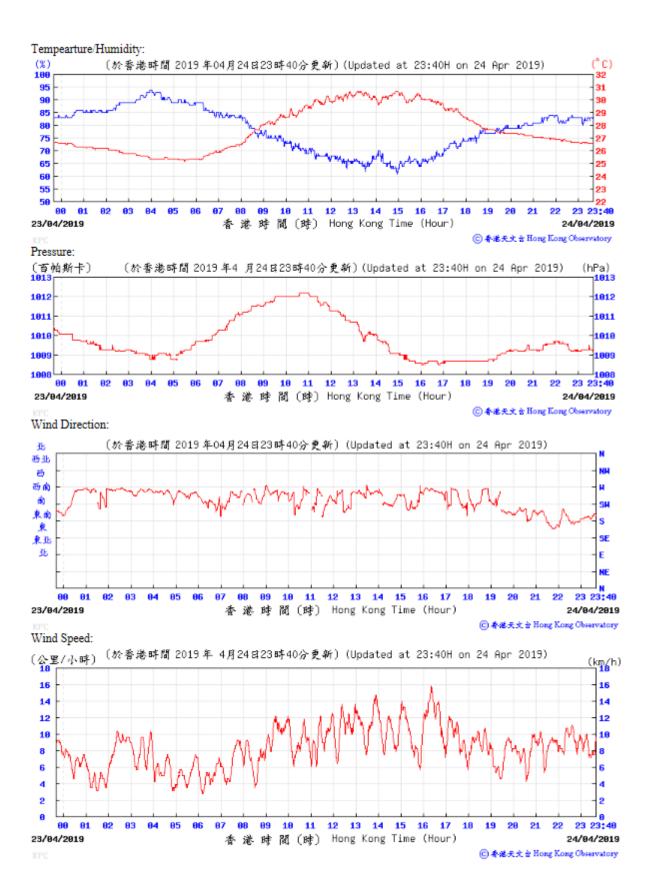

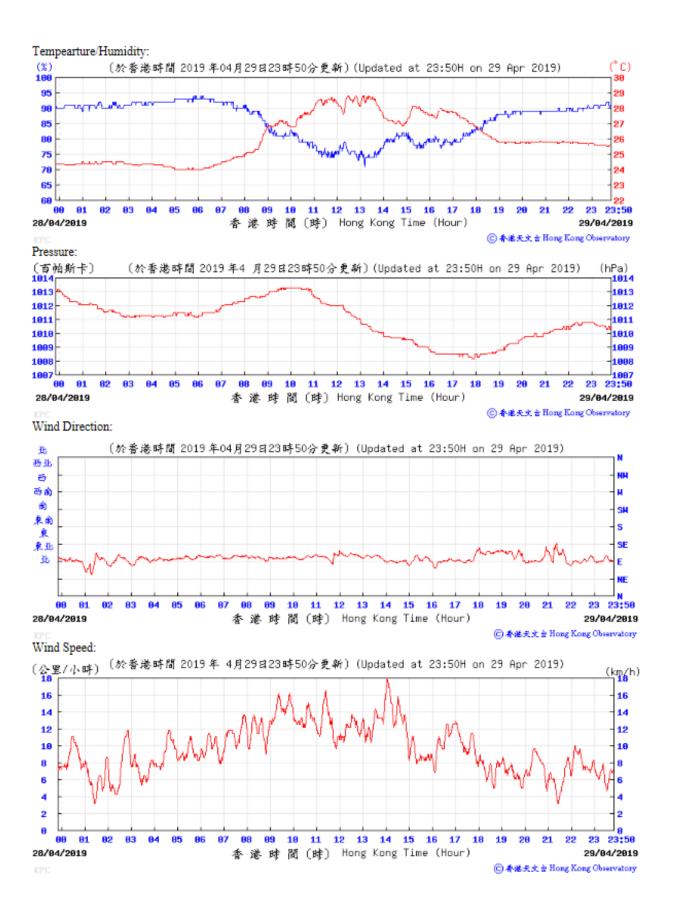

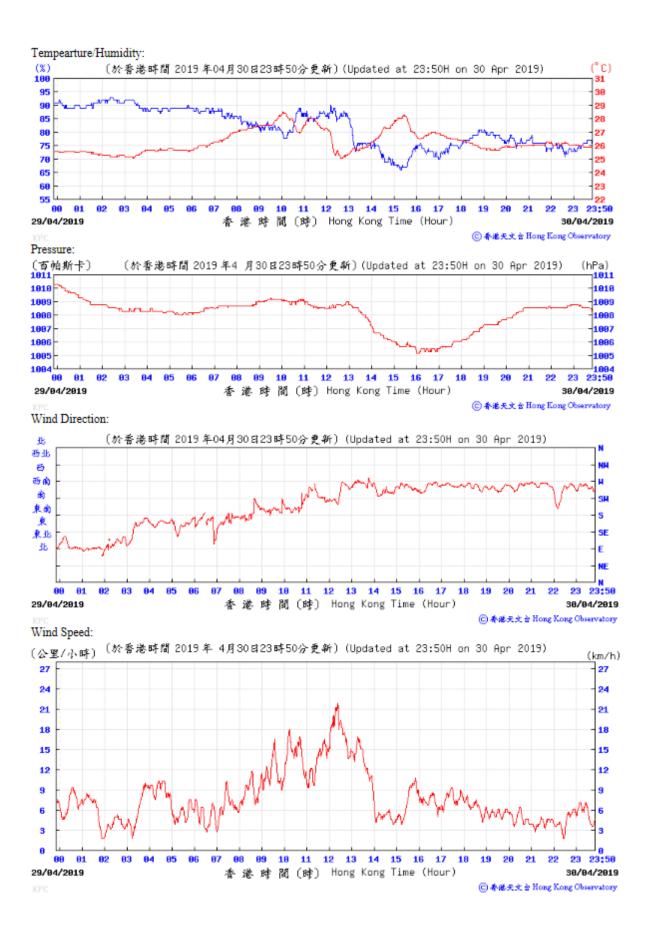

I. Waste Flow table

M+ Museum

Table I-1: Monthly Waste Flow Table for M+ Museum

		Actual Qua	antities of Ine	rt C&D Mate	rials Generat	ed Monthly		Actual Quantities of C&D Wastes Generated Monthly						
Month	Total Quantity Generated	Hard Rocks and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Disposed to Sorting Facility	Imported Fill	Metals	Paper/ Cardboard Packaging	Plastics	Wood/ Timber	Chemical Waste	Others, e.g. General Refuse	
	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	
2015					•						•	•		
Nov	46607.4	0.0	0.0	8240.0	38367.4	0.0	0.0	76.2	0.0	0.0	0.0	0.0	67.6	
Dec	29652.9	0.0	0.0	29621.4	31.5	0.0	0.0	26.3	0.0	0.0	0.0	1.0	66.0	
Sub-total (2015)	76260.3	0.0	0.0	37861.4	38398.9	0.0	0.0	102.5	0.0	0.0	0.0	1.0	133.6	
2016														
Jan	21077.4	0.0	6352.0	14576.0	149.4	0.0	0.0	18.8	0.0	0.0	0.0	0.0	23.2	
Feb	7626.2	0.0	3424.0	4048.0	154.2	0.0	0.0	59.8	0.0	0.0	0.0	0.0	20.5	
Mar	10442.5	0.0	1600.0	7888.0	954.5	0.0	0.0	29.7	0.0	0.0	0.0	0.0	46.3	
Apr	30413.2	0.0	6352.0	23408.0	653.2	0.0	0.0	25.8	0.1	0.0	27.8	0.0	34.5	
May	24083.5	0.0	112.0	23216.0	755.5	0.0	0.0	61.5	0.4	0.0	33.6	0.0	62.3	
Jun	7880.1	0.0	4736.0	2384.0	760.1	0.0	0.0	106.6	0.1	0.0	14.6	0.0	52.8	
Jul	5893.1	0.0	2656.0	2240.0	997.1	0.0	0.0	77.6	0.0	0.0	33.6	0.0	83.1	
Aug	13709.6	0.0	0.0	12432.0	1277.6	0.0	0.0	111.3	0.2	0.0	38.5	0.0	104.9	
Sep	6702.0	0.0	0.0	5648.0	1000.1	53.9	0.0	104.2	0.0	0.0	45.5	0.2	107.9	
Oct	2103.6	0.0	0.0	496.0	1595.4	12.2	0.0	83.0	0.4	0.0	73.5	0.0	108.2	
Nov	3302.7	0.0	0.0	2384.0	855.5	63.2	0.0	88.4	0.6	0.0	63.0	0.0	129.1	
Dec	899.8	0.0	0.0	736.0	126.8	37.0	0.0	48.3	0.6	0.0	70.0	0.0	89.0	
Sub-total (2016)	134133.5	0.0	25232.0	99456.0	9279.3	166.3	0.0	814.9	2.3	0.0	400.1	0.2	861.8	
2017														
Jan	675.2	0.0	0.0	432.0	237.9	5.3	0.0	79.5	1.0	0.0	70.0	0.0	79.7	
Feb	927.7	0.0	0.0	768.0	125.6	34.0	0.0	70.5	0.6	0.0	84.0	0.0	81.4	
Mar	1856.7	0.0	0.0	1280.0	466.9	109.8	0.0	62.8	0.4	0.0	98.0	0.0	148.5	
Apr	642.4	0.0	0.0	160.0	324.9	157.5	0.0	87.5	0.7	0.0	175.0	0.0	102.5	
May	1118.2	0.0	0.0	528.0	416.4	173.7	0.0	118.3	0.0	0.0	280.0	0.0	139.0	
Jun	650.0	0.0	0.0	0.0	451.6	198.4	0.0	199.7	1.4	0.0	350.0	0.0	98.7	
Jul	1762.0	0.0	0.0	0.0	1466.6	295.4	0.0	36.9	1.2	0.0	244.0	0.0	164.2	
Aug	1231.5	0.0	0.0	0.0	867.5	364.0	0.0	50.9	0.9	0.0	59.0	0.0	186.9	
Sep	1681.7	0.0	0.0	0.0	1342.0	339.7	0.0	52.3	0.7	0.0	77.0	0.0	265.3	
Oct	483.6	0.0	0.0	0.0	242.5	241.1	0.0	374.8	0.6	0.0	24.1	0.0	128.5	
Nov	822.8	0.0	0.0	0.0	344.5	478.3	0.0	948.5	0.7	0.0	140.0	0.2	219.1	
Dec	601.3	0.0	0.0	0.0	236.2	365.1	0.0	903.6	0.8	0.0	320.0	0.0	241.9	

	Actual Quantities of Inert C&D Materials Generated Monthly							Actual Quantities of C&D Wastes Generated Monthly						
Month	Total Quantity Generated	Hard Rocks and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Disposed to Sorting Facility	Imported Fill	Metals	Paper/ Cardboard Packaging	Plastics	Wood/ Timber	Chemical Waste	Others, e.g. General Refuse	
	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	
Sub-total (2017)	12453.0	0.0	0.0	3168.0	6522.6	2762.4	0.0	2985.3	8.9	0.0	1921.1	0.2	1855.5	
2018														
Jan	1015.3	0.0	0.0	0.0	574.1	441.2	0.0	773.3	1.5	0.0	100.0	0.0	183.6	
Feb	847.6	0.0	0.0	0.0	608.3	239.3	0.0	34.0	1.0	0.0	25.0	0.0	154.9	
Mar	1507.0	0.0	0.0	0.0	1102.1	404.9	0.0	39.5	1.5	0.0	120.0	0.0	264.1	
Apr	2942.8	0.0	0.0	0.0	2542.4	400.4	0.0	60.1	0.3	0.0	100.0	0.0	252.5	
May	2109.2	0.0	0.0	0.0	1593.3	515.9	0.0	37.0	0.4	0.0	70.0	0.0	311.4	
Jun	1697.6	0.0	0.0	0.0	1162.4	535.2	0.0	47.0	0.3	0.0	105.0	0.0	188.2	
Jul	945.5	0.0	0.0	0.0	646.1	299.4	0.0	15.2	0.4	0.0	150.0	0.0	277.6	
Aug	730.8	0.0	0.0	0.0	461.4	269.4	0.0	0.0	0.0	0.0	40.0	0.0	109.1	
Sep	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	
Oct	1193.1	0.0	0.0	0.0	895.7	297.5	0.0	129.3	2.7	0.0	200.0	0.0	116.6	
Nov	1608.9	0.0	0.0	0.0	841.1	767.7	0.0	45.8	1.1	0.0	245.0	0.0	213.9	
Dec	1143.4	0.0	0.0	0.0	341.9	801.5	0.0	256.7	0.8	0.0	180.0	0.0	198.2	
Sub-total (2018)	15741.0	0.0	0.0	0.0	10768.7	4972.3	0.0	1437.9	9.9	0.0	1335.0	0.0	2270.2	
2019												•		
Jan	1478.9	0.0	0.0	0.0	572.3	906.6	0.0	192.1	0.8	0.0	40.0	0.0	303.9	
Feb	618.5	0.0	0.0	0.0	397.4	221.2	0.0	43.4	1.2	0.0	20.0	0.0	429.7	
Mar	1102.2	0.0	0.0	0.0	908.9	193.2	0.0	31.8	0.0	0.0	20.0	0.0	645.2	
Apr	327.4	0.0	0.0	0.0	127.3	200.2	0.0	0.0	0.0	0.0	300.0	0.9	477.4	
Sub-total (2019)	3527.0	0.0	0.0	0.0	2005.8	1521.2	0.0	267.3	2.0	0.0	380.0	0.9	1856.2	
Total	242114.8	0.0	25232.0	140485.4	66975.2	9422.2	0.0	5607.8	23.2	0.0	4036.2	2.2	6977.3	

Note:

- 127.3 tonnes of inert C&D material were disposed of as public fill to Tseung Kwan O Area 137 Public Fill respectively in the reporting month.

- For inert C&D materials reused in other projects, the projects refer to (1) Green Valley; (2) Advance Works for Shek Wu Hui Sewage Treatment Works (3) Design and Construction of Kai Tak Cable Tunnel, CLP; (4) MTR Contract 1002 Whampoa Station and Overrun Tunnel; (5) CEDD Tuen Mun Area 54 Contract No. CV/2015/03; (6) Union Construction Ltd.'s site; (7) Foundation Works at Marriot Hotel at Ocean Park.

- Quantities of waste materials generated for the previous reporting months have been updated by Contractor.

Lyric Theatre Complex

Table I-2: Monthly Waste Flow Table for Lyric Theatre Complex

		Actual Qu	uantities of Ine	ert C&D Mater	ials Generate	d Monthly		Actual Quantities of C&D Wastes Generated Monthly						
Month	Total Quantity Generated	Hard Rocks and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Disposed to Sorting Facilty	Imported Fill	Metals	Paper/ Cardboard Packaging	Plastics	Wood/ Timber	Chemical Waste	Others, e.g. General Refuse	
	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	
2016		-												
Mar	2702.1	0.0	0.0	0.0	2702.1	0.0	0.0	4.5	0.1	0.0	0.0	0.0	30.6	
Apr	8631.5	0.0	0.0	0.0	8631.5	0.0	0.0	16.0	0.0	0.0	0.0	0.0	19.2	
May	12487.8	0.0	0.0	0.0	12487.8	0.0	0.0	34.0	0.0	0.0	0.0	0.7	60.5	
Jun	8600.8	0.0	0.0	0.0	8600.8	0.0	0.0	31.4	0.2	0.0	0.0	0.5	13.5	
Jul	12624.2	0.0	0.0	0.0	12624.2	0.0	0.0	19.6	0.0	0.0	0.0	2.0	9.9	
Aug	14419.9	0.0	0.0	0.0	14419.9	0.0	0.0	43.9	0.0	0.0	0.0	0.0	11.1	
Sep	13671.3	0.0	0.0	0.0	13671.3	0.0	0.0	59.8	0.0	0.0	0.0	1.6	12.4	
Oct	13088.9	0.0	0.0	0.0	13088.9	0.0	0.0	36.9	0.2	1.5	0.0	0.0	15.2	
Nov	12424.7	0.0	0.0	0.0	12424.7	0.0	0.0	74.7	0.0	0.0	0.0	1.4	10.2	
Dec	12487.6	0.0	0.0	0.0	12487.6	0.0	0.0	13.9	0.0	0.0	0.0	1.3	9.0	
Sub-total (2016)	111138.8	0.0	0.0	0.0	111138.8	0.0	0.0	334.5	0.4	1.5	0.0	7.6	191.6	
2017														
Jan	9607.8	0.0	0.0	0.0	9607.8	0.0	0.0	29.5	0.0	0.0	0.0	0.0	7.3	
Feb	9108.2	0.0	0.0	0.0	9108.2	0.0	0.0	50.2	0.2	0.0	0.0	0.7	9.8	
Mar	11361.7	0.0	0.0	0.0	11361.7	0.0	0.0	16.1	0.0	0.0	0.0	1.4	8.5	
Apr	2591.5	0.0	0.0	0.0	2591.5	0.0	0.0	35.7	0.0	0.0	0.0	0.0	4.7	
May	2579.3	0.0	0.0	99.0	2480.3	0.0	0.0	20.9	0.1	0.0	0.0	0.5	10.0	
Jun	476.0	0.0	0.0	341.0	129.7	5.3	0.0	0.0	0.0	0.0	0.0	0.0	7.6	
Jul	3419.0	0.0	0.0	804.0	2615.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	17.8	
Aug	3730.9	0.0	0.0	1377.5	2353.4	0.0	0.0	0.0	0.0	0.0	0.0	0.0	4.4	
Sep	2108.2	0.0	0.0	1133.5	974.7	0.0	0.0	34.6	0.2	0.0	0.0	0.0	10.8	
Oct	9159.0	0.0	0.0	7868.0	1291.0	0.0	0.0	0.0	0.0	0.0	0.0	0.7	9.3	
Nov	5095.4	0.0	0.0	4352.0	725.2	18.1	0.0	0.0	0.0	0.0	0.0	0.0	38.8	
Dec	3856.2	0.0	0.0	3076.0	780.2	0.0	0.0	0.0	0.2	0.0	0.0	0.4	8.4	
Sub-total (2017)	63093.1	0.0	0.0	19051.0	44018.7	23.4	0.0	187.1	0.7	0.0	0.0	3.8	137.3	

		Actual Qu	uantities of Ine	ert C&D Mater	rials Generate	d Monthly			Actual Quant	ities of C&D \	Wastes Gener	ated Monthly	
Month	Total Quantity Generated	Hard Rocks and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Disposed to Sorting Facilty	Imported Fill	Metals	Paper/ Cardboard Packaging	Plastics	Wood/ Timber	Chemical Waste	Others, e.g. General Refuse
	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)	(in tonnes)
2018													
Jan	4083.7	0.0	0.0	1455.0	2628.7	0.0	0.0	0.0	0.0	0.0	0.0	0.0	2.9
Feb	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	1.2
Mar	6120.2	0.0	0.0	5782.0	338.2	0.0	0.0	0.0	0.0	1.0	0.0	0.5	17.6
Apr	14460.3	0.0	0.0	12484.1	1976.3	0.0	0.0	0.0	0.0	0.2	0.0	0.0	7.6
May	59783.7	0.0	0.0	46989.0	12794.7	0.0	0.0	59.6	0.0	0.0	0.0	0.0	9.4
Jun	53117.5	0.0	0.0	37642.8	15474.7	0.0	0.0	51.5	0.2	0.0	0.0	0.0	12.8
Jul	89901.5	0.0	0.0	85317.1	4584.4	0.0	165.1	114.6	0.0	0.0	0.0	0.0	41.3
Aug	35137.3	0.0	0.0	33731.6	1405.7	0.0	214.3	148.1	0.0	0.0	0.0	0.0	48.5
Sep	4815.3	0.0	0.0	4619.1	109.2	87.0	174.6	40.0	0.0	0.0	0.0	0.0	179.2
Oct	19021.9	0.0	0.0	11301.0	7564.7	156.1	0.0	106.3	0.4	0.0	0.0	0.0	450.4
Nov	104165.3	0.0	0.0	79811.6	24348.4	5.3	0.0	54.5	0.0	0.6	0.0	0.0	28.9
Dec	62987.1	0.0	0.0	51284.4	11697.1	5.6	0.0	95.1	0.0	0.6	0.0	0.0	63.1
Sub-total (2018)	453593.7	0.0	0.0	370417.7	82922.0	254.0	553.9	669.7	0.5	2.4	0.0	0.5	862.7
2019		•	•		•								
Jan	74479.1	0.0	0.0	69249.5	5229.7	0.0	318.0	326.7	0.2	0.0	0.0	0.0	76.3
Feb	21969.9	0.0	0.0	17723.9	4246.0	0.0	16.5	55.2	0.0	0.0	0.0	0.0	26.7
Mar	14394.7	0.0	0.0	5666.3	8728.4	0.0	337.8	64.5	0.0	0.0	0.0	0.0	36.3
Apr	28673.9	0.0	0.0	21394.3	7279.6	0.0	0.0	32.6	0.0	0.8	0.0	0.0	24.9
Sub-total (2019)	139517.6	0.0	0.0	114034.0	25483.7	0.0	672.3	479.0	0.2	0.8	0.0	0.0	164.2
Total	768569.5	0.0	0.0	503502.7	263563.1	277.4	1226.3	1670.2	1.8	4.7	0.0	11.9	1355.8

Note:

- 5,835.39 tonnes and 1,444.18 tonnes of inert C&D material were disposed of as public fill to Tseung Kwan O Area 137 and Tuen Mun Area 38 Public Fill respectively in the reporting month.

J. Environmental Mitigation Measures – Implementation Status

Table J-1: Environmental Mitigation Measures Implementation Status

		Impleme	entation Stage
EM&A Ref.	Recommendation Measures	M+ Museum	Lyric Theatre Complex
Air Quality I	mpact (Construction)		
2.1 &	General Dust Control Measures		
10.3.1	Frequent water spraying for active construction areas (12 times a day or once every one hour), including Heavy construction activities such as construction of buildings or roads, drilling, ground excavation, cut and fill operations (i.e., earth moving)	~	\checkmark
2.1 &	Best Practice For Dust Control		
10.3.1	The relevant best practices for dust control as stipulated in the Air Pollution Control (construction Dust) Regulation should be adopted to further reduce the construction dust impacts from the Project. These best practices include:		
	Good Site Management		
	 Good site management is important to help reducing potential air quality impact down to an acceptable level. As a general guide, the Contractor should maintain high standard of housekeeping to prevent emission of fugitive dust. Loading, unloading, handling and storage of raw materials, wastes or by- products should be carried out in a manner so as to minimise the release of visible dust emission. Any piles of materials accumulated on or around the work areas should be cleaned up regularly. Cleaning, repair and maintenance of all plant facilities within the work areas should be carried out in a manner minimising generation of fugitive dust emissions. The material should be handled properly to prevent fugitive dust emission before cleaning. 	Obs	✓
	Disturbed Parts of the Roads		
	 Each and every main temporary access should be paved with concrete, bituminous hardcore materials or metal plates and kept clear of dusty materials; or 	\checkmark	\checkmark
	 Unpaved parts of the road should be sprayed with water or a dust suppression chemical so as to keep the entire road surface wet. 	✓	\checkmark
	Exposed Earth		
	 Exposed earth should be properly treated by compaction, hydroseeding, vegetation planting or seating with latex, vinyl, bitumen within six months after the last construction activity on the site or part of the site where the exposed earth lies. 	N/A	N/A
	Loading, Unloading or Transfer of Dusty Materials		
	All dusty materials should be sprayed with water immediately prior to any loading or transfer operation	√	\checkmark

		Implementation Stage				
EM&A Ref.	Recommendation Measures	M+ Museum	Lyric Theatre Complex			
	so as to keep the dusty material wet.					
	Debris Handling					
	 Any debris should be covered entirely by impervious sheeting or stored in a debris collection area sheltered on the top and the three sides. 	\checkmark	\checkmark			
	 Before debris is dumped into a chute, water should be sprayed so that it remains wet when it is dumped. 	\checkmark	\checkmark			
	Transport of Dusty Materials		✓			
	 Vehicle used for transporting dusty materials/spoils should be covered with tarpaulin or similar material. The cover should extend over the edges of the sides and tailboards. 	v	·			
	Wheel washing	,				
	 Vehicle wheel washing facilities should be provided at each construction site exit. Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels. 	\checkmark	\checkmark			
	Use of vehicles					
	 The speed of the trucks within the site should be controlled to about 10km/hour in order to reduce adverse dust impacts and secure the safe movement around the site. 	\checkmark	4			
	 Immediately before leaving the construction site, every vehicle should be washed to remove any dusty materials from its body and wheels. 	\checkmark	\checkmark			
	 Where a vehicle leaving the construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle. 	✓	\checkmark			
	Site hoarding					
	 Where a site boundary adjoins a road, street, service lane or other area accessible to the public, hoarding of not less than 2.4m high from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit. 	✓	\checkmark			
.1 &	Best Practicable Means for Cement Works (Concrete Batching Plant)					
0.3.1	The relevant best practices for dust control as stipulated in the Guidance Note on the Best Practicable Means for Cement Works (Concrete Batching Plant) BPM 3/2(93) should be followed and implemented to further reduce the construction dust impacts of the Project. These best practices include:					
	Exhaust from Dust Arrestment Plant					

		Implementation Stage				
EM&A Ref.	Recommendation Measures	M+ Museum	Lyric Theatre Complex			
	 Wherever possible the final discharge point from particulate matter arrestment plant, where is not necessary to achieve dispersion from residual pollutants, should be at low level to minimise the effect on the local community in the case of abnormal emissions and to facilitate maintenance and inspection 	~	\checkmark			
	Emission Limits					
	All emissions to air, other than steam or water vapour, shall be colourless and free from persistent mist or smoke	\checkmark	\checkmark			
	Engineering Design/Technical Requirements					
	 As a general guidance, the loading, unloading, handling and storage of fuel, raw materials, products, wastes or by-products should be carried out in a manner so as to prevent the release of visible dust and/or other noxious or offensive emissions 	✓	✓			
	Non-Road Mobile Machinery (NRMM):					
	All NRMMs operating on-site which are subject to emission control of Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation are approved/exempted (as the case may be) and affixed with the requisite approval/exemption labels.	\checkmark	\checkmark			
voise Impa	ct (Construction)					
3.1 & 10.4.1	Good Site Practice Good site practice and noise management can significantly reduce the impact of construction site activities on nearby NSRs. The following package of measures should be followed during each phase of construction:					
	 only well-maintained plant to be operated on-site and plant should be serviced regularly during the construction works; 	Obs	\checkmark			
	 machines and plant that may be in intermittent use to be shut down between work periods or should be throttled down to a minimum; 	\checkmark	\checkmark			
	 plant known to emit noise strongly in one direction, should, where possible, be orientated to direct noise away from the NSRs; 	\checkmark	\checkmark			
	mobile plant should be sited as far away from NSRs as possible; and	\checkmark	\checkmark			
	 material stockpiles and other structures to be effectively utilised, where practicable, to screen noise from on-site construction activities. 	\checkmark	\checkmark			
.1 &	Adoption of Quieter PME					
0.4.1	The recommended quieter PME adopted in the assessment were taken from the EPD's QPME Inventory and "Sound Power Levels of Other Commonly Used PME" are presented in Table 4.26 in the EIA report. It	\checkmark	\checkmark			

		Impleme	entation Stage
EM&A Ref.	Recommendation Measures	M+ Museum	Lyric Theatre Complex
3.1 & 10.4.1	Use of Movable Noise Barriers Movable noise barriers can be very effective in screening noise from particular items of plant when constructing the Project. Noise barriers located along the active works area close to the noise generating component of a PME could produce at least 10 dB(A) screening for stationary plant and 5 dB(A) for mobile plant provided the direct line of sight between the PME and the NSRs is blocked.	N/A	✓
3.1 & 10.4.1	Use of Noise Enclosure/ Acoustic Shed The use of noise enclosure or acoustic shed is to cover stationary PME such as air compressor and concrete pump. With the adoption of the noise enclosure, the PME could be completely screened, and noise reduction of 15 dB(A) can be achieved according to the EIAO Guidance Note No.9/2010.	N/A	N/A
3.1 & 10.4.1	Use of Noise Insulating Fabric Noise insulating fabric can also be adopted for certain PME (e.g. drill rig, pilling machine etc). The fabric should be lapped such that there are no openings or gaps on the joints. According to the approved Tsim Sha Tsui Station Northern Subway EIA report (AEIAR-127/2008), a noise reduction of 10 dB(A) can be achieved for the PME lapped with the noise insulating fabric.	N/A	\checkmark
3.1 & 10.4.1	Scheduling of Construction Works outside School Examination Periods During construction phase, the contractor should liaise with the educational institutions (including NSRs LCS and CRGPS) to obtain the examination schedule and avoid the noisy construction activities during school examination periods.	N/A	N/A
Water Quali	y Impact (Construction)		
4.1 &	Construction site runoff and drainage		
10.5.1	The site practices outlined in ProPECC Note PN 1/94 should be followed as far as practicable in order to minimise surface runoff and the chance of erosion. The following measures are recommended to protect water quality and sensitive uses of the coastal area, and when properly implemented should be sufficient to adequately control site discharges so as to avoid water quality impacts:		
	 At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels, earth bunds or sand bag barriers should be provided on site to direct storm water to silt removal facilities. The design of the temporary on-site drainage system should be undertaken by the WKCDA's Contractor prior to the commencement of construction; 	\checkmark	\checkmark
	 Sand/silt removal facilities such as sand/silt traps and sediment basins should be provided to remove sand/silt particles from runoff to meet the requirements of the TM standards under the WPCO. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC Note PN 1/94. Sizes may vary depending upon the flow rate. The detailed design of the sand/silt traps should be undertaken by the WKCDA's Contractor prior to the commencement of construction. 	V	v
	• All drainage facilities and erosion and sediment control structures should be regularly inspected and	Obs	Obs

		implementation Stage	
EM&A Ref.	Recommendation Measures	M+ Museum	Lyric Theatre Complex
	maintained to ensure proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit should be regularly removed, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times.		
	 Measures should be taken to minimize the ingress of site drainage into excavations. If excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from foundation excavations should be discharged into storm drains via silt removal facilities. 	✓	✓
	 All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facility should be provided at construction site exit where practicable. Wash-water should have sand and silt settled out and removed regularly to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. 	✓	✓
	 Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system. 	✓	✓
	 Manholes (including newly constructed ones) should be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and stormwater runoff being directed into foul sewers. 	\checkmark	\checkmark
	 Precautions should be taken at any time of the year when rainstorms are likely. Actions should be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC Note PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes. 	✓	\checkmark
	 Bentonite slurries used in piling or slurry walling should be reconditioned and reused wherever practicable. Temporary enclosed storage locations should be provided on-site for any unused bentonite that needs to be transported away after all the related construction activities are completed. The requirements in ProPECC Note PN 1/94 should be adhered to in the handling and disposal of bentonite slurries. 	N/A	N/A
	Barging facilities and activities		
	Recommendations for good site practices during operation of the proposed barging point include:		
	 All vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; 	N/A	N/A
	 Loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water. Barges or hoppers should not be filled to a level that will cause the overflow of 	N/A	N/A

Implementation Stage

		Implementation Stage	
EM&A Ref.	Recommendation Measures	M+ Museum	Lyric Theatre Complex
	 materials or polluted water during loading or transportation; All hopper barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material; and Construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site. 	N/A N/A	N/A N/A
4.1 &	Sewage effluent from construction workforce		
10.5.1	Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to handle sewage from the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.	√	\checkmark
4.1 &	General construction activities		
10.5.1	 Construction solid waste, debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering any nearby storm water drain. Stockpiles of cement and other construction materials should be kept covered when not being used. 	\checkmark	\checkmark
	 Oils and fuels should only be stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to any nearby storm water drain, all fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event. 	1	\checkmark
Waste Mana	gement Implications (Construction)		
6.1 &	Good Site Practices		
10.7.1	Recommendations for good site practices during the construction activities include:		
	 Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site 	\checkmark	\checkmark
	 Training of site personnel in proper waste management and chemical handling procedures 	\checkmark	\checkmark
	 Provision of sufficient waste disposal points and regular collection of waste 	\checkmark	\checkmark
	• Appropriate measures to minimise windblown litter and dust/odour during transportation of waste by either covering trucks or by transporting wastes in enclosed containers	\checkmark	\checkmark
	 Provision of wheel washing facilities before the trucks leaving the works area so as to minimise dust introduction to public reade. 	\checkmark	\checkmark
	 introduction to public roads Well planned delivery programme for offsite disposal such that adverse environmental impact from transporting the inert or non-inert C&D materials is not anticipated 	\checkmark	\checkmark
6.1 &	Waste Reduction Measures		
10.7.1	Recommendations to achieve waste reduction include:		

	Implementation Stage	
Recommendation Measures	M+ Museum	Lyric Theatre Complex
Sort inert C&D material to recover any recyclable portions such as metals	\checkmark	✓
 Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal 	\checkmark	\checkmark
 Encourage collection of recyclable waste such as waste paper and aluminium cans by providing separate labelled bins to enable such waste to be segregated from other general refuse generated by the work force 	✓	4
Proper site practices to minimise the potential for damage or contamination of inert C&D materials	\checkmark	\checkmark
 Plan the use of construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste 	\checkmark	\checkmark
Inert and Non-inert C&D Materials		
In order to minimise impacts resulting from collection and transportation of inert C&D material for off-site disposal, the excavated materials should be reused on-site as fill material as far as practicable. In addition, inert C&D material generated from excavation works could be reused as fill materials in local projects that require public fill for reclamation.	✓	✓
• The surplus inert C&D material will be disposed of at the Government's PFRFs for beneficial use by		
	\checkmark	\checkmark
 Laison with the CEDD Public Fill Committee (PFC) on the allocation of space for disposal of the inert C&D materials at PFRF is underway. No construction work is allowed to proceed until all issues on management of inert C&D materials have been resolved and all relevant arrangements have been endorsed by the relevant authorities including PFC and EPD. 	V	✓
 The C&D materials generated from general site clearance should be sorted on site to segregate any inert materials for reuse or disposal of at PFRFs whereas the non-inert materials will be disposed of at the designated landfill site. 	\checkmark	~
 In order to monitor the disposal of inert and non-inert C&D materials at respectively PFRFs and the designated landfill site, and to control fly-tipping, it is recommended that the Contractor should follow the Technical Circular (Works) No.6/2010 for Trip Ticket System for Disposal of Construction & Demolition Materials issued by Development Bureau. In addition, it is also recommended that the Contractor should prepare and implement a Waste Management Plan detailing their various waste arising and waste management practices in accordance with the relevant requirements of the Technical Circular (Works) No. 19/2005 Environmental Management on Construction Site. 	~	~
Chemical Waste		
 If chemical wastes are produced at the construction site, the Contractor will be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the "Code of Practice on 		
	 Sort inert C&D material to recover any recyclable portions such as metals Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal Encourage collection of recyclable waste such as waste paper and aluminium cans by providing separate labelled bins to enable such waste to be segregated from other general refuse generated by the work force Proper site practices to minimise the potential for damage or contamination of inert C&D materials Plan the use of construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste Inert and Non-inert C&D Materials In order to minimise impacts resulting from collection and transportation of inert C&D material for off-site disposal, the excavated materials should be reused on-site as fill material as far as practicable. In addition, inert C&D material will be disposed of at the Government's PFRFs for beneficial use by other projects in Hong Kong. Liaison with the CEDD Public Fill Committee (PFC) on the allocation of space for disposal of the inert C&D materials an PFRF is underway. No construction work is allowed to proceed until all issues on management of inert C&D materials in decal PFRFs whereas the non-inert materials will be disposed of at the Government's PFRFs and the designated landfill site. The CAD materials agnerated from general site clearance should be sorted on site to segregate any inert materials for teuso of at PFRFs whereas the non-inert materials are reused of at the designated landfill site. In order to monitor the disposal of at PFRFs whereas the non-inert materials will be disposed of at the designated landfill site. In order to monitor the disposal of at PFRFs whereas the non-inert materials of the segregate any inert materials for reuse or disposal of at PFRFs whereas the n	Recommendation Measures M+ Museum 9. Sort inert C&D material to recover any recyclable portions such as metals • 9. Segregation and storage of different types of waste in different containers or skips to enhance reuse or recycling of materials and their proper disposal • 9. Encourage collection of recyclable waste such as waste paper and aluminium cans by providing separate labelled bins to enable such waste to be segregated from other general refuse generated by the work force • 9. Proper site practices to minimise the potential for damage or contamination of inert C&D materials • 10. Proper site practices to minimise the potential for dramage or contamination of inert C&D materials • 10. Proper site practices to minimise the potentials carefully to minimise amount of waste generated and avoid unnecessary generation of waste • 11. Order to minimise impacts resulting from collection and transportation of inert C&D material for off-site disposal to recearation works could be reused as fill materials in local projects that require public fill for reclamation. • 11. The surplus inert C&D material will be disposed of at the Government's PFRFs for beneficial use by other projects in Hong Kong. • 12. Liaison with the CEDD Public Fill Committee (PFC) on the allocation of space for disposal of the inert C&D materials at PFRF is underway. No construction work is allowed to proceed until all issues on management of inert C&D materials have been resolved and all relevant atranspentents will be disposed of at the designated landfill site. •

		Implementation Stage	
EM&A Ref.	Recommendation Measures	M+ Museum	Lyric Theatre Complex
	the Packaging Labelling and Storage of Chemical Wastes". Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor should use a licensed collector to transport and dispose of the chemical wastes at the approved Chemical Waste Treatment Centre or other licensed recycling facilities, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Obs	Obs
	 Potential environmental impacts arising from the handling activities (including storage, collection, transportation and disposal of chemical waste) are expected to be minimal with the implementation of appropriate mitigation measures as recommended. 	\checkmark	~
6.1 &	General Refuse		
10.7.1	General refuse should be stored in enclosed bins or compaction units separated from inert C&D materials. A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from inert C&D materials. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.	\checkmark	\checkmark
Land Conta	mination (Construction)		
7.1 & 10.8.1	The potential for land contamination issues at the TST Fire Station due to its future relocation will be confirmed by site investigation after land acquisition. Where necessary, mitigation measures for minimising potential exposure to contaminated materials (if any) or remediation measures will be identified. If contaminated land is identified (e.g., during decommissioning of fuel oil storage tanks) after the commencement of works, mitigation measures are proposed in order to minimise the potentially adverse effects on the health and safety of construction workers and impacts arising from the disposal of potentially contaminated materials.		
	The following measures are proposed for excavation and transportation of contaminated material:		
	 To minimize the chance for construction workers to come into contact with any contaminated materials, bulk earth-moving excavation equipment should be employed; 	N/A	N/A
	• Contact with contaminated materials can be minimised by wearing appropriate clothing and personal protective equipment such as gloves and masks (especially when interacting directly with	N/A	N/A
	contaminated material), provision of washing facilities and prohibition of smoking and eating on site;	N/A	N/A N/A
	 Stockpiling of contaminated excavated materials on site should be avoided as far as possible; The use of contaminated soil for landscaping purpose should be avoided unless pre-treatment was carried out; 	N/A	N/A
	• Vehicles containing any contaminated excavated materials should be suitably covered to reduce dust	N/A	N/A

		Implementation Stage	
EM&A Ref.	Recommendation Measures	M+ Museum	Lyric Theatre Complex
	emissions and/or release of contaminated wastewater;	N/A	N/A
	 Truck bodies and tailgates should be sealed to stop any discharge; Only licensed waste haulers should be used to collect and transport contaminated material to treatment/disposal site and should be equipped with tracking system to avoid fly tipping; 	N/A	N/A
	Speed control for trucks carrying contaminated materials should be exercised;	N/A	N/A
	 Observe all relevant regulations in relation to waste handling, such as Waste Disposal Ordinance (Cap 354), Waste Disposal (Chemical Waste) (General) Regulation (Cap 354) and obtain all necessary permits where required; and 	N/A	N/A
	 Maintain records of waste generation and disposal quantities and disposal arrangements. 	N/A	N/A
Ecological Ir	npact (Construction)		
	No mitigation measure is required.		
Landscape a	and Visual Impact (Construction)		
Table 9.1 & 10.8 (CM1)	Trees should be retained in situ on site as far as possible. Should tree removal be unavoidable due to construction impacts, trees will be transplanted or felled with reference to the stated criteria in the Tree Removal Applications to be submitted to relevant government departments for approval in accordance to ETWB TCW No. 29/2004 and 3/2006.	N/A	N/A
Table 9.1 & 10.8 (CM2)	Compensatory tree planting shall be incorporated to the proposed project and maximize the new tree, shrubs and other vegetation planting to compensate tree felled and vegetation removed. Also, implementation of compensatory planting should be of a ratio not less than 1:1 in terms of quality and quantity within the site.	N/A	N/A
Table 9.1 & 10.8 (CM3)	Buffer trees for screening purposes to soften the hard architectural and engineering structures and facilities.	N/A	N/A
Table 9.1 & 10.8 (CM4)	Softscape treatments such as vertical green wall panel /planting of climbing and/or weeping plants, etc, to maximize the green coverage and soften the hard architectural and engineering structures and facilities.	N/A	N/A
Table 9.1 & 10.8 (CM5)	Roof greening by means of intensive and extensive green roof to maximize the green coverage and improve aesthetic appeal and visual quality of the building/structure.	N/A	N/A
Table 9.1 & 0.8 (CM6)	Sensitive streetscape design should be incorporated along all new roads and streets.	N/A	N/A
Table 9.1 & 0.8 (CM7)	Structure, ornamental planting shall be provided along amenity strips to enhance the landscape quality.	N/A	N/A
Table 9.1 & 10.8 (CM8)	Landscape design shall be incorporated to architectural and engineering structures in order to provide aesthetically pleasing designs.	N/A	N/A

		Implementation Stage		
EM&A Ref.	Recommendation Measures	M+ Museum	Lyric Theatre Complex	
Table 9.1 (CM9)	Minimize the structure of marine facilities to be built on the seabed and foreshore in order to minimize the affected extent to the waterbody	N/A	N/A	
Table 9.2 & 10.9 (MCP1)	Use of decorative screen hoarding/boards	✓	4	
Table 9.2 & 10.9 (MCP2)	Early introduction of landscape treatments	N/A	N/A	
Table 9.2 & 10.9 (MCP3)	Adoption of light colour for the temporary ventilation shafts for the basement during the transition period.	N/A	N/A	
Table 9.2 & 10.9 (MCP4)	Control of night time lighting	✓	\checkmark	
Table 9.2 & 10.9 (MCP5)	Use of greenery such as grass cover for the temporary open areas will help achieve the visual balance and soften the hard edges of the structures.	N/A	N/A	

N/A - Not Applicable

✓ - Implemented

Obs - Observed

Rem - Reminder

K. Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Cumulative statistics for complaints, notifications of summons and successful prosecutions for the Project account for period starting from the date of commencement of construction works (i.e. 31 October 2015 for M+ Museum main works and 1 March 2016 for Lyric Theatre Complex) to the end of the reporting month and are summarised in the **Table K-1** and **Table K-2** below respectively.

Table K-1: Statistics for complaints, notifications of summons and successful prosecutions for M+ Museum Main Works

Reporting Period	Cumulative Statistics			
	Complaints	Notifications of summons	Successful prosecutions	
This reporting month	0	0	0	
From 31 October 2015 to end of the reporting month	6	1	0	

Table K-2: Statistics for complaints, notifications of summons and successful prosecutions for Lyric Theatre Complex

Reporting Period	Cumulative Statistics			
	Complaints	Notifications of summons	Successful prosecutions	
This reporting month	0	0	0	
From 1 March 2016 to end of the reporting month	8	0	0	
