



**JOB No.: TCS00881/18 & TCS00944/18**

**SITE FORMATION AND ASSOCIATED INFRASTRUCTURAL  
WORKS FOR DEVELOPMENT OF COLUMBARIUM,  
CREMATORIUM AND RELATED FACILITIES AT SANDY  
RIDGE CEMETERY**

**MONTHLY ENVIRONMENTAL MONITORING AND AUDIT  
REPORT (NO.55) – FEBRUARY 2023**

**PREPARED FOR  
HSIN CHONG TSUN YIP JOINT VENTURE &  
SANG HING CIVIL CONTRACTORS CO., LTD**

<b>Date</b>	<b>Reference No.</b>	<b>Prepared By</b>	<b>Certified By</b>
14 March 2023	TCS00881/18/600/R0722v2		
		Nicola Hon (Environmental Consultant)	Tam Tak Wing (Environmental Team Leader)

<b>Version</b>	<b>Date</b>	<b>Remarks</b>
1	10 March 2023	First Submission
2	14 March 2023	Amended according to the IEC's comments

Our Ref: TCS00881/18/300/L0726

**Civil Engineering and Development Department**  
2/F, Civil Engineering and Development Building,  
101 Princess Margaret Rd,  
Homantin, Kowloon

**Attn: Mr. SHUM Ngai Hung, Steven**

**14 March 2023**

By e-mail

Dear Sirs,

**Re: Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery  
Monthly Environmental Monitoring & Audit Report (No.55) – February 2023**

---

We confirmed that the captioned report has complied with the requirement set out in the EM&A Manual, we hereby certify the captioned report pursuant to Specific Condition 3.4 of the Environmental Permit No. FEP-01/534/2017/A and EP-534/2017/A.

Should you have any queries, please feel free to contact the undersigned at Tel: 2959-6059 or Fax: 2959-6079 or Email: [twtam@fordbusiness.com](mailto:twtam@fordbusiness.com).

Yours sincerely,

For and on Behalf of

**Action-United Environmental Services & Consulting (AUES)**



T. W. Tam  
Environmental Team Leader  
TW/nh

cc

ARUP (RE of Contracts 1 and 2)	Mr. Anthony Lau	by e-mail
HCTY-JV (Contractor of Contract 1)	Mr. Ho Man To	by e-mail
Sang Hing (Contractor of Contract 2)	Mr. Elvin Lam	by e-mail
Acuity (IEC)	Mr. Jacky Leung	by e-mail

Our Ref.: PL-202303022

Hsin Chong Tsun Yip Joint Venture (CV/2016/10)  
Hsin Chong Centre  
107 – 109 Wai Yip Street  
Kwun Tong, Kowloon  
Hong Kong

Attention: Mr. HO Man-to

14 March 2023

Dear Sir,

**Site Formation and Associated Infrastructural Works for Development of Columbarium at  
Sandy Ridge Cemetery  
Monthly Environmental Monitoring and Audit Report (No. 55) February 2023**

I refer to the email of the ET regarding the captioned Monthly Report. According to Section 3.4 of the EP-534/2017/A and the FEP-01/534/2017/A, I hereby verify the Monthly EM&A Report for February 2023 (Version 2) with Ref. No. TCS00881/18/600/R0722v2.

You are required to follow up the comments from EPD and IEC on the relevant EPs requirement and provide supplementary information of this report for our further review as soon as possible.

Yours faithfully,



Leung CH Jacky  
Independent Environmental Checker

## EXECUTIVE SUMMARY

ES.01. This is the **55<sup>th</sup>** Monthly Environmental Monitoring and Audit (EM&A) Report summarizing the monitoring results and inspection findings under the Project for the period from **1<sup>st</sup> to 28<sup>th</sup> February 2023** (the Reporting Month).

### ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES.02. In the Reporting Month, the major construction works under the Project included Contract CV/2016/10 (hereinafter named “Contract 1”) and Contract CV/2017/02 (hereinafter named “Contract 2”). Environmental monitoring activities under the EM&A programme in this Reporting Month are summarized in the following table.

**Table ES-1 Summary of EM&A Programme in the Reporting Month**

Issues	Environmental Monitoring Parameters / Inspection	Monitoring Locations		Total Occasions/dates
		CV/2016/10	CV/2017/02	
Air Quality	1-hour TSP	ASR-1	ASR-2	36
	24-hour TSP		ASR-3	15
Construction Noise	L <sub>eq</sub> (30min) Daytime	CN-1 CN-2	CN-3 CN-4	12
Water Quality	In-situ measurement and Water sampling	M3	M1, M2 and M4	12
Ecology	Sensitive Habitat	Transect within site area of CV/2016/10	Transect within site area of CV/2017/02	11 <sup>th</sup> Feb 2023
Landscape & Visual	Site Inspection	Site area of CV/2016/10	Site area of CV/2017/02	28 <sup>th</sup> Feb 2023
Inspection & Audit	Environmental Team (ET) Regular Environmental Site Inspection	Site area of CV/2016/10	Site area of CV/2017/02	4
	Independent Environmental Checker (IEC) Monthly Environmental Site Audit			1

### BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES.03. In the Reporting Month, no exceedance of air quality and water quality monitoring was recorded. No noise complaint (which triggered Action Level) was received and Limit Level exceedance for noise monitoring exceedance was recorded. The statistics of environmental exceedance, Notification and investigation of exceedance are summarized in the following table.

**Table ES-2 Breach of Action and Limit (A/L) Levels in the Reporting Month**

Environmental Issues	Monitoring Parameters	Action Level	Limit Level	Event & Action	
				Investigation Findings	Corrective Actions
Air Quality	1-hour TSP	0	0	-	-
	24-hour TSP	0	0	-	-
Construction Noise	Leq <sub>30min</sub> Daytime	0	0	-	-
Water Quality	DO	0	0	-	-
	Turbidity	0	0	-	-
	Suspended Solids (SS)	0	0		

ES.04. Monthly ecological monitoring for sensitive habitat for area of Contract 1 and Contract 2 were undertaken on **11<sup>th</sup> February 2023**. After analysing survey results in February from 2019 to 2023, there was no significant drop in species richness and abundance for wetland and non-wetland habitat for area of Contract 1, but a decrease in species richness and abundance for wetland and non-wetland habitat for area of Contract 2. Yet, good site practice during construction, with reference to EM&A Manual, is required to prevent or alleviate environmental impacts. For instance, the size of work

areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. In addition, implementing proper waste disposal is necessary to reduce contamination to water and soil. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.

- ES.05. In the Reporting Period, there was no vegetation clearance for both Contract 1 and Contract 2, and precautionary check for the presence of nesting birds was not required to carry out.
- ES.06. Landscape and visual inspection at both Contracts were undertaken on **28<sup>th</sup> February 2023**. The Contractor was reminded to prevent the construction material pile within Tree Protection Zone and ensure no works is allowed within the TPZ.

**ENVIRONMENTAL COMPLAINT**

- ES.07. No environmental summons or successful prosecution was recorded in this Reporting Month. The statistics of summons or successful prosecutions are summarized in the following tables.

**Table ES-3 Environmental Complaint Summaries in the Reporting Month**

Reporting Month		Environmental Complaint Statistics		
		Frequency	Cumulative	Complaint Nature
1 <sup>st</sup> – 28 <sup>th</sup> February 2023	Contract 1	0	2	(1) Air Quality (1) Noise
	Contract 2	0	5	(1) Water (2) Air Quality (1) Noise (1) soil/ muddy water

**NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS**

- ES.08. No environmental summons or successful prosecution was recorded in this Reporting Month. The statistics of summons or successful prosecutions are summarized in the following tables.

**Table ES-4 Environmental Summons Summaries in the Reporting Month**

Reporting Month		Environmental Summons Statistics		
		Frequency	Cumulative	Summons Nature
1 <sup>st</sup> – 28 <sup>th</sup> February 2023	Contract 1	0	0	NA
	Contract 2	0	0	NA

**Table ES-5 Environmental Prosecution Summaries in the Reporting Month**

Reporting Month		Environmental Prosecution Statistics		
		Frequency	Cumulative	Prosecution Nature
1 <sup>st</sup> – 28 <sup>th</sup> February 2023	Contract 1	0	0	NA
	Contract 2	0	0	NA

- ES.09. In addition, no complaint and emergency event relating to violation of environmental legislation for illegal dumping and landfilling was received.

**REPORTING CHANGE**

- ES.010. No reporting change was made in the Reporting Month.

**SITE INSPECTION**

- ES.011. In the Reporting Month, joint site inspections for Contract 1 to evaluate the site environmental performance were carried out by the Resident Engineer, ET and the Contractor of the Contract 1 on **2<sup>nd</sup>, 9<sup>th</sup>, 16<sup>th</sup>, and 23<sup>rd</sup> February 2023**. Moreover, joint site inspections for Contract 2 by the RE, ET and the Contractor of Contract 2 were carried out **2<sup>nd</sup>, 9<sup>th</sup>, 16<sup>th</sup>, and 23<sup>rd</sup> February 2023**. IEC attended joint site inspection for both Contracts on **16<sup>th</sup> February 2023**. No non-compliance was noted during the site inspections.

**FUTURE KEY ISSUES**

- ES.012. During dry season, the Contractors are reminded to pay special attention on the air quality mitigation measures such as wheel wash facilities, watering of haul roads, loose soil construction surface and covering of dusty materials with tarpaulin sheet should be implemented as far as practicable.
- ES.013. Water quality mitigation measures as recommended in the EM&A Manual should be fully implemented, in particular to prevent surface runoff and other pollutants from flowing to local stream and Conservation Area.
- ES.014. Construction noise would be a key environmental issue during construction phase of the Project. Noise mitigation measures such as using quiet plants and mobile noise barriers should be implemented in accordance with the EM&A requirement.

## Table of Contents

<b>1. INTRODUCTION</b>	<b>1</b>
1.1 PROJECT BACKGROUND	1
1.2 REPORT STRUCTURE	2
<b>2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS</b>	<b>4</b>
2.1 CONSTRUCTION CONTRACT PACKAGING	4
2.2 CONSTRUCTION PROGRESS	4
2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS	4
2.4 SUMMARY OF SUBMISSION UNDER THE ENVIRONMENTAL PERMIT REQUIREMENTS	5
<b>3. SUMMARY OF IMPACT MONITORING REQUIREMENT</b>	<b>7</b>
3.1 GENERAL	7
3.2 MONITORING PARAMETERS	7
3.3 MONITORING LOCATIONS	7
3.4 MONITORING FREQUENCY AND PERIOD	9
3.5 MONITORING EQUIPMENT	9
3.6 EQUIPMENT CALIBRATION	12
3.7 DATA MANAGEMENT AND DATA QA/QC CONTROL	12
3.8 DETERMINATION OF ACTION/LIMIT (A/L) LEVELS	12
<b>4. AIR QUALITY</b>	<b>14</b>
4.1 MONITORING RESULTS	14
4.2 AIR MONITORING EXCEEDANCE	14
<b>5. CONSTRUCTION NOISE</b>	<b>15</b>
5.1 MONITORING RESULTS	15
5.2 NOISE MONITORING EXCEEDANCE	15
<b>6. WATER QUALITY</b>	<b>16</b>
6.1 MONITORING RESULTS	16
6.2 WATER QUALITY MONITORING EXCEEDANCE	17
<b>7. ECOLOGY MONITORING</b>	<b>18</b>
7.1 REQUIREMENT	18
7.2 METHODOLOGY	18
7.3 ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 1)	19
7.4 ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 2)	21
7.5 MONITORING OF FLORA SPECIES OF CONSERVATION INTEREST	22
7.6 MEASURE FOR PROTECTION OF NESTING BIRD	22
<b>8. LANDSCAPE AND VISUAL</b>	<b>23</b>
8.1 REQUIREMENT	23
8.2 FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH	23
<b>9. WASTE MANAGEMENT</b>	<b>24</b>
9.1 GENERAL WASTE MANAGEMENT	24
9.2 RECORDS OF WASTE QUANTITIES	24
<b>10. SITE INSPECTION</b>	<b>25</b>
10.1 REQUIREMENT	25
10.2 FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH	25
<b>11. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE</b>	<b>26</b>
11.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	26
<b>12. IMPLEMENTATION STATUS OF MITIGATION MEASURES</b>	<b>27</b>
12.1 GENERAL REQUIREMENTS	27
12.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH	28
12.3 KEY ISSUES FOR THE COMING MONTH	28
<b>13. CONCLUSIONS AND RECOMMENDATIONS</b>	<b>30</b>
13.1 CONCLUSIONS	30
13.2 RECOMMENDATIONS	30

**LIST OF TABLES**

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS FOR CONTRACT 1
TABLE 2-2	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS FOR CONTRACT 2
TABLE 2-3	STATUS OF SUBMISSION AS UNDER FEP FOR CONTRACT 1
TABLE 2-4	STATUS OF SUBMISSION AS UNDER FEP FOR CONTRACT 2
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	DESIGNATED AIR QUALITY MONITORING LOCATION UNDER THE PROJECT
TABLE 3-3	DESIGNATED CONSTRUCTION NOISE MONITORING LOCATION UNDER THE PROJECT
TABLE 3-4	DESIGNATED WATER QUALITY MONITORING STATIONS UNDER THE PROJECT
TABLE 3-5	AIR QUALITY MONITORING EQUIPMENT
TABLE 3-6	NOISE MONITORING EQUIPMENT
TABLE 3-7	WATER QUALITY MONITORING EQUIPMENT
TABLE 3-8	ACTION AND LIMIT LEVELS FOR AIR QUALITY MONITORING
TABLE 3-9	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 3-10	ACTION AND LIMIT LEVELS FOR WATER QUALITY
TABLE 4-1	SUMMARY OF AIR QUALITY MONITORING RESULTS AT ASR-1 UNDER CONTRACT 1
TABLE 4-2	SUMMARY OF AIR QUALITY MONITORING RESULTS AT ASR-2 UNDER CONTRACT 2
TABLE 4-3	SUMMARY OF AIR QUALITY MONITORING RESULTS AT ASR-3A UNDER CONTRACT 2
TABLE 5-1	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS UNDER CONTRACT 1
TABLE 5-2	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS UNDER CONTRACT 2
TABLE 6-1	SUMMARY OF WATER QUALITY MONITORING RESULTS – M3 UNDER CONTRACT 1
TABLE 6-2	SUMMARY OF WATER QUALITY MONITORING RESULTS (M1, M2 AND M4) UNDER CONTRACT 2
TABLE 6-3	SUMMARY OF FIELD MEASUREMENTS FOR WATER QUALITY
TABLE 6-4	ACTION AND LIMIT (A/L) LEVELS EXCEEDANCE RECORD
TABLE 6-5	SUMMARY OF INVESTIGATION OF WATER QUALITY EXCEEDANCE IN THE REPORTING MONTH
TABLE 7-1	ACTION AND LIMIT LEVELS FOR WET WOODLAND HABITATS MONITORING
TABLE 7-2	ACTION AND LIMIT LEVELS FOR NON-WET WOODLAND HABITATS MONITORING
TABLE 7-3	SCHEDULE OF FAUNAL SURVEYS IN EACH YEAR DURING CONSTRUCTION PHASE
TABLE 7-4	RESULT OF FAUNAL SURVEY UNDER CONTRACT 1
TABLE 7-5	RESULT OF FRESHWATER COMMUNITIES SURVEY UNDER CONTRACT 1
TABLE 7-6	RESULT OF FAUNAL SURVEY UNDER CONTRACT 2
TABLE 7-7	RESULT OF FRESHWATER COMMUNITIES SURVEY UNDER CONTRACT 2
TABLE 8-1	LANDSCAPE & VISUAL INSPECTION FINDING FOR CONTRACT 1
TABLE 8-2	LANDSCAPE & VISUAL INSPECTION FINDING FOR CONTRACT 2
TABLE 9-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 9-2	SUMMARY OF QUANTITIES OF C&D WASTES
TABLE 10-1	SITE OBSERVATIONS FOR THE WORKS OF CONTRACT 1
TABLE 10-2	SITE OBSERVATIONS FOR THE WORKS OF CONTRACT 2
TABLE 11-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 11-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 11-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 12-1	ENVIRONMENTAL MITIGATION MEASURES
TABLE 12-2	WORK UNDERTAKEN AND MITIGATION MEASURES FOR CONTRACT 1
TABLE 12-3	WORK UNDERTAKEN AND MITIGATION MEASURES FOR CONTRACT 2



## **LIST OF APPENDICES**

APPENDIX A	LAYOUT PLAN OF THE PROJECT
APPENDIX B	ORGANIZATION STRUCTURE AND CONTACT DETAILS OF RELEVANT PARTIES
APPENDIX C	THREE MONTHS ROLLING PROGRAMME
APPENDIX D	DESIGNATED MONITORING LOCATIONS
APPENDIX E	CALIBRATION CERTIFICATES OF MONITORING EQUIPMENT AND LABORATORY CERTIFICATE
APPENDIX F	EVENT AND ACTION PLAN OF AIR QUALITY, NOISE AND WATER QUALITY
APPENDIX G	MONITORING SCHEDULES OF THE REPORTING MONTH AND COMING MONTH
APPENDIX H	MONITORING DATA OF 24-HOUR TSP AIR QUALITY, NOISE AND WATER QUALITY
APPENDIX I	GRAPHICAL PLOTS OF AIR QUALITY, NOISE AND WATER QUALITY
APPENDIX J	METEOROLOGICAL DATA OF THE REPORTING MONTH
APPENDIX K	ECOLOGICAL SURVEY REPORT
APPENDIX L	LANDSCAPE & VISUAL INSPECTION CHECKLIST
APPENDIX M	MONTHLY SUMMARY WASTE FLOW TABLE
APPENDIX N	COMPLAINT LOG
APPENDIX O	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)
APPENDIX P	ILLUSTRATIONS OF SITE ACTIVITIES

## 1. INTRODUCTION

### 1.1 PROJECT BACKGROUND

1.1.1 Civil Engineering and Development Department (CEDD) is the Project Proponent for the Project “*Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery*”. The Project is a Designated Project to be implemented under Environmental Permit No. EP-534/2017/A and FEP-01/534/2017/A. The layout plan of the Project is shown in [Appendix A](#). Major works to be executed under the Project shall include to the following:

Designated Works under EP-534/2017/A

- (i) Site formation of about 5.5 hectares of land and associated drainage, sewerage and landscape works for development of Columbarium and Crematorium facilities at the Sandy Ridge Cemetery;
- (ii) Construction of a new road (about 800m) connecting the Crematorium and Man Kam To Road and the pick-up/drop-off point at Man Kam To Road;
- (iii) Widening two sections of the existing Sha Ling Road (about 900m and 500m respectively);
- (iv) Widening of about 1.4km of the existing Lin Ma Hang Road; and
- (v) Improvement works to the existing barging point at Siu Lam (the barging point is rejected by Tuen Mun DC and no improvement works required)

Designated Works under FEP-01/534/2017/A

- (i) Site formation works for a formed platform of about 1.8 hectares and associated drainage, sewerage and landscape works for development of Columbarium at the Sandy Ridge Cemetery;
- (ii) Construction of the pick-up/drop-off point at Man Kam To Road;
- (iii) Widening of 900m of the existing Sha Ling Road;
- (iv) Improvement works to the existing barging point at Siu Lam (the barging point is rejected by Tuen Mun DC and no improvement works required)

1.1.2 To facilitate the Project management, the Project works were separated into three Contracts to be executed which are described in below sub-sections.

1.1.3 *Contract No. CV/2016/10 – Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery* (hereinafter named “Contract 1”):-

- Site formation of about 1.77 ha of land for the proposed pick-up and drop-off area for shuttle bus operation;
- Upgrading of a section of 900m existing Sha Ling Road from 3m wide carriageway to 7.3m wide carriageway with footpath at both sides;
- Construction of one EVA with a total length of about 160m;
- Construction of noise barriers along Sha Ling Road;
- Modification of junction between Man Kam To Road and Sha Ling Road;
- Construction of a new pick up / drop off point at Man Kam To Road;
- Relocation and construction of a new refuse collection point near junction between Man Kam To Road and Sha Ling Road;
- Associated geotechnical works including cut and fill slopes, soil nailing works and retaining structures;
- Associated drainage, sewerage and waterworks along Sha Ling Road; and
- Associated landscaping works.

1.1.4 *Contract No. CV/2017/02 – Infrastructural Works at Man Kam To Road and Lin Ma Hang Road for Development of Columbarium at Sandy Ridge Cemetery* (hereinafter named “Contract 2”):-

- Construction of a new road connecting Columbarium site to Crematorium site;
- Construction of one EVA with a total length of about 300m;
- Widening of a section of 1.4 km long Lin Ma Hang Road (between Man Kam To Road and Ping Yuen River) from 6m wide carriageway to 7.3m with 2m width footpath on both sides;
- Provision of a pair of lay-by at Lin Ma Hang Road;
- Construction of a new vehicular access connecting the Sheung Shui Landmark North PTI and Lung Sum Avenue;

- Construction of covered walkway along Fanling Station Road;
- Removal of planters and central divider along Fanling Station Road and San Wan Road;
- Associated drainage, sewerage, waterworks and utility works along Man Kam To Road and Lin Ma Hang Road;
- Associated geotechnical works including cut and fill slopes, soil nailing works and retaining structures; and
- Associated landscaping works.

1.1.5 *CEDD Contract No. (to be confirmed):-*

- Site Formation for the platform of the columbarium site;
- Construction of two 2 at-grade access roads;
- Construction of road junction between Man Kam To Road and the new access road;
- Associated drainage, sewerage and waterworks along the two new access roads;
- Associated geotechnical works including cut and fill slopes, soil nailing works and retaining structures; and
- Associated landscaping works

1.1.6 Hsin Chong Tsun Yip Joint Venture (hereafter referred as “HCTYJV”) has been awarded Contract 1 on 5 December 2017. According to the Contract requirement, HCTYJV shall take over the responsibility for part of the Environmental Permit No. EP-534/2017 for ease of management, therefore application for Further Environmental Permit was submitted by HCTYJV to EPD on 26 January 2018 and Further Environmental Permit No. FEP-01/534/2017 was granted to HCTYJV by EPD on 23 February 2018. Furthermore, EPD issued Environmental Permit No. FEP-01/534/2017/A on 24 December 2018.

1.1.7 Sang Hing Civil Contractors Company Limited (hereinafter referred as “Sang Hing”) was awarded Contract 2 on 23 May 2018. The Contract Works is a Designated Project as under Environmental Permit (EP) No. EP-534/2017. Furthermore, EPD issued Environmental Permit No. EP-534/2017/A on 24 December 2018.

1.1.8 Action-United Environmental Services & Consulting (AUES) has been commissioned by the Contractors as an Environmental Team (ET) to implement the Environmental Monitoring and Audit (EM&A) programme in accordance with the approved EM&A Manual as well as the associated duties. As part of the EM&A programme, baseline monitoring to determine the ambient environmental conditions was completed before construction work commencement. The Baseline Monitoring Report (air, noise and water) certified by ET Leader (ETL) and verified by Independent Environmental Checker (IEC) was submitted to Environmental Protection Department (EPD) and it was approved by EPD on 25 October 2018.

1.1.9 Major construction work of Contract 1 and Contract 2 was commenced on 16 August 2018 and 5 November 2018 respectively.

1.1.10 This is the 55<sup>th</sup> Monthly EM&A Report summarizing the monitoring results and inspection findings for the period from 1<sup>st</sup> to 28<sup>th</sup> February 2023.

## 1.2 REPORT STRUCTURE

1.2.1 The Monthly EM&A Report is structured into the following sections:-

- Section 1** *Introduction*
- Section 2** *Project Organization and Construction Progress*
- Section 3** *Summary of Monitoring Requirements*
- Section 4** *Air Quality Monitoring Results*
- Section 5** *Noise Monitoring Results*
- Section 6** *Water Quality Monitoring Results*
- Section 7** *Ecology Monitoring Results*
- Section 8** *Landscape & Visual*
- Section 9** *Waste Management*
- Section 10** *Site Inspections*

- Section 11** *Environmental Complaints and Non-Compliance*
- Section 12** *Implementation Status of Mitigation Measures*
- Section 13** *Conclusions and Recommendation*

## 2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

### 2.1 CONSTRUCTION CONTRACT PACKAGING

2.1.1 To facilitate the project management and implementation, the Project was divided by the following contracts:

- Contract 1 (Contract No. CV/2016/10)
- Contract 2 (Contract No. CV/2017/02)
- Contract 3 (Contract No. TBA)

2.1.2 Organization structure and contact details of relevant parties with respect to on-site environmental management are shown in [Appendix B](#).

### 2.2 CONSTRUCTION PROGRESS

2.2.1 The three-month rolling construction programme for Contract 1 and Contract 2 are enclosed in [Appendix C](#). Construction activities of the Contract 1 and Contract 2 undertaken in the Reporting Month are presented below.

#### Contract 1 (CV/2016/10)

- Installation of Type 2 railing and street lighting
- Paving block installation works

#### Contract 2 (CV/2017/02)

- Construction of footpath at Lin Ma Hang Road
- Watermain pipe and sewer installation at Man Kam To Road North Slow Lane
- Construction of road works at Sandy Ridge

### 2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.3.1 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project in this Reporting Month is presented in [Tables 2-1 and 2-2](#).

**Table 2-1 Status of Environmental Licenses and Permits for Contract 1**

Item	Description	License/ Permit ref no.	License/ Permit Status
1	Air Pollution Control (Construction Dust) Regulation	Ref. no. 428909 Acknowledged by EPD on 20/12/2017	Valid
2	Chemical waste Producer Registration	WPN: 5231-641-H3937-01 Issued by EPD on 27/03/2018	Valid
3	Water Pollution Control Ordinance	License no. WT00030795-2018 Issued date: 9/5/2018 Expire Date: 31/5/2023	Valid
4	Billing Account for Disposal of Construction Waste	Account no.: 7029769	Valid

**Table 2-2 Status of Environmental Licenses and Permits for Contract 2**

Item	Description	License/ Permit ref no.	License/ Permit Status	
1	Air Pollution Control (Construction Dust) Regulation	Ref. no. 440406 Acknowledged by EPD on 14/12/2018	Man Kam To Road (near Sha Ling Road to Kong Nga Po Road)	Valid
		Ref. no. 440405 Acknowledged by EPD on 14/12/2018	Fanling Station Road	Valid
		Ref. no. 440404 Acknowledged by EPD on 14/12/2018	Sa Ling Road (Sandy Ridge Cemetery)	Valid
		Ref. no. 440401	Lin Ma Hang Road	Valid

Item	Description	License/ Permit ref no.	License/ Permit Status
		Acknowledged by EPD on 14/12/2018 (San Uk Ling – Muk Wu Nga Yiu)	
		Ref. no. 440402 Acknowledged by EPD on 14/12/2018 Lung Sum Avenue (near Landmark North)	Valid
2	Chemical waste Producer Registration	WPN: 5213-641-S4151-01 Issued by EPD on 04/02/2019	Valid
3	Water Pollution Control Ordinance	License no: WT00032936-2018 Issued date: 16/01/2019 Expire Date: 31/01/2024 Man Kam To Road & Lin Ma Hang Road, Man Kam To	Valid
		License no: WT00033335-2019 Issued date: 29/03/2019 Expire Date: 31/03/2024 Columbarium at Sandy Ridge Cemetery	Valid
		License no: WT00034717-2019 Issued date: 9/10/2019 Expire Date: 31/10/2024 Fanling Station Road	Valid
4	Billing Account for Disposal of Construction Waste	Account no.: 7031098	Valid

## 2.4 SUMMARY OF SUBMISSION UNDER THE ENVIRONMENTAL PERMIT REQUIREMENTS

2.4.1 **Tables 2-3 to 2-4** summarized the submission status under the EP and/or FEP stipulation in the Reporting Month.

**Table 2-3 Status of Submission as under FEP**

Item	EP and / or FEP Stipulation	Description	Status
1	Condition 2.10 of FEP	Management organization of : i) the main construction companies; ii) ET; and iii) IEC and the supporting team	Submitted and no approval is required.
2	Condition 2.11 of FEP	i) Detailed phasing programme of all construction works; and ii) Location plan of all construction works	Submitted and no approval is required.
3	Condition 2.12 of FEP	Contamination Assessment Plan (CAP)	Approved by EPD on 27 May 2019
4	Condition 2.13 of FEP	Grassland Reinstatement Plan	Pending approval
5	Condition 2.14 to 2.16 of FEP	Vegetation Survey Report and Vegetation Transplantation Proposal for Contract 1	Approved by EPD on 12 October 2018
6	Condition 2.17 of FEP	Woodland Compensation Plan (Rev.05)	Approved by EPD on 30 Jun 2020
7	Condition 2.18 of FEP	Monitoring and Survey Plan for Golden-headed Cisticola for Contract 1 (Rev.02)	Approved by EPD on 22 Oct 2019
8	Condition 2.20 of FEP	Landscape & Visual Mitigation and Tree Preservation Plan(s) Contract 1 (Rev.04)	Pending approval
9	Condition 2.22 of FEP	Traffic Noise Mitigation Plan Contract 1 (Rev. 4)	Pending approval
10	Condition 3.3 of the FEP	Baseline Monitoring Report (Air, Noise and Water)	Approved by EPD on 25 October 2018
11	Condition 4.2 of the FEP	The Contract Internet website	Internet website address has notified EPD on 15 Jun 2018

Item	EP and / or FEP Stipulation	Description	Status
			and no approval is required.

**Table 2-4 Status of Submission as under EP**

Item	EP and / or FEP Stipulation	Description	Status
1	Condition 2.10 of EP	Management organization of : i) the main construction companies; ii) ET; and iii) IEC and the supporting team	Submitted and no approval is required.
2	Condition 2.11 of EP	i) Detailed phasing programme of all construction works; and ii) Location plan of all construction works	Submitted and no approval is required.
3	Condition 2.12 of EP	Layout Plan for the proposed footpath at Lin Ma Hang Road	Approved by EPD on 25 April 2022
4	Condition 2.13 of EP	Contamination Assessment Plan (CAP)	Approved by EPD on 27 May 2019
5	Condition 2.14 of EP	Grassland Reinstatement Plan	Pending approval
6	Condition 2.15 to 2.17 of EP	Vegetation Survey Report and Vegetation Transplantation Proposal under Contract 2	Approved by EPD on 15 June 2022
7	Condition 2.18 of EP	Woodland Compensation Plan (Rev.05)	Approved by EPD on 30 Jun 2020
8	Condition 2.19 of EP	Monitoring and Survey Plan for Golden-headed Cisticola Contract 2	Approved by EPD on 9 Nov 2022
9	Condition 2.21 – 2.22 of EP	Landscape & Visual Mitigation and Tree Preservation Plan(s) Contract 2	Pending approval
10	Condition 2.23 of EP	Traffic Noise Mitigation Plan Contract 2	Pending approval
11	Condition 3.3 of the EP	Baseline Monitoring Report (Air, Noise and Water)	Approved by EPD on 25 October 2018
12	Condition 4.2 of the EP	The Contract Internet website	Internet website address has notified EPD on 15 June 2018 and no approval is required.

### 3. SUMMARY OF IMPACT MONITORING REQUIREMENT

#### 3.1 GENERAL

3.1.1 The EM&A requirements are set out in the Approved EM&A Manual. Environmental issues such as air quality, construction noise, water quality and ecology were identified as the key issues during the construction phase of the Project.

3.1.2 A summary of construction phase EM&A requirements are presented in the sub-sections below.

#### 3.2 MONITORING PARAMETERS

3.2.1 The EM&A impact monitoring shall cover the following environmental aspect:

- Air quality;
- Construction noise;
- Water quality;
- Ecology; and
- Landscape and visual

3.2.2 A summary of the monitoring parameters is presented in *Table 3-1* below

**Table 3-1 Summary of EM&A Requirements**

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> <li>• 1-hour TSP;</li> <li>• 24-hour TSP</li> </ul>
Noise	<ul style="list-style-type: none"> <li>• Leq<sub>(30min)</sub> during normal working hours.; and</li> <li>• Leq<sub>(15min)</sub> during the construction works undertaken in Restricted Hours</li> </ul>
Water Quality	<b>In-situ Measurements</b> <ul style="list-style-type: none"> <li>• Dissolved Oxygen Concentration (mg/L) &amp; Saturation (% );</li> <li>• Temperature (°C);</li> <li>• Turbidity (NTU);</li> <li>• Salinity (ppm)</li> <li>• pH unit;</li> <li>• Water depth (m); and</li> <li>• Stream Flow Velocity (m/sec).</li> </ul>
	<b>Laboratory Analysis</b> <ul style="list-style-type: none"> <li>• Suspended Solids (mg/L)</li> </ul>
Ecology	Ecologically sensitive habitats (wetland habitats and non-wetland habitats)

#### 3.3 MONITORING LOCATIONS

3.3.1 According to the Approved EM&A Manual of the Project – *Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery*, the designated monitoring locations for air quality, noise, water quality and ecology under the monitoring programme, is shown in *Appendix D*.

3.3.2 Since the Project was divided into three Works Contracts and all Contracts will be commenced at different time, the construction phase impact monitoring will only be performed at the Contract-related monitoring stations upon commencement of each Contract Works.

##### Air Quality

3.3.3 There were three (3) designated air quality monitoring stations recommended in the Approved EM&A Manual Section 5.6.1.1. There was proposed relocation of air quality monitoring location ASR-3 in October 2018 since the landlord refused to set up the HVS at his premises and nearby Conservation Area due to noise nuisance and Muk Wu Nga Yiu House No. 2A was proposed as alternative location ASR-3a. The proposal dated on 9 November 2018 which verified by IEC was submitted to EPD for approval. Based on rationale in Section 3.3.2, the Contract-related air quality monitoring location for construction phase were summarized in *Table 3-2* and illustrated in *Appendix D*.



**Table 3-2 Designated Air Quality Monitoring Location under the Project**

Location ID	Description in EM&A Manual	Location	Related Work Contract
ASR-1	Village House along Man Kam To Road	Sha Ling Village House No.6	Contract 1
ASR-2	Village House at San Uk Ling	San Uk Ling Village House No.1	Contract 2
ASR-3	Village House at Muk Wu Nga Yiu	Muk Wu Nga Yiu House No.28	Contract 2
ASR-3a (#)	Village House at Muk Wu Nga Yiu	Muk Wu Nga Yiu House No.2A	Contract 2

*Remark: (#) There was proposed relocation of air quality monitoring location ASR-3 in October 2018. The proposal dated on 9 November 2018 after verified by IEC was submitted to EPD for approval.*

- 3.3.4 If the designated monitoring location is required to relocate, alternative monitoring location shall agree with IEC and seek for EPD approval which shall meet the following criteria:
- i) Be at the site boundary or such locations close to the major dust emission source;
  - ii) Close to the sensitive receptors;
  - iii) Take into account the prevailing meteorological conditions;
  - iv) For monitoring location located in the vicinity of the ASRs, care shall be taken to cause minimal disturbance to the occupants during monitoring.
  - v) When positioning the HVS, the following points shall be noted:
    - a. a horizontal platform with appropriate support to secure the samples against gusty wind shall be provided;
    - b. no two samplers shall be placed less than 2m apart;
    - c. the distance between the HVS and an obstacle, such as buildings, must be at least twice the height that the obstacle protrudes above the HVS;
    - d. a minimum of 2 m separation from walls, parapets and penthouses is required for HVS at the rooftop;
    - e. a minimum of 2 m separation from any supporting structure, measures horizontally is required;
    - f. no furnace or incinerator flue is nearby;
    - g. airflow around the sampler is unrestricted;
    - h. the HVS is more than 20 m from the dripline;
    - i. any wire fence and gate to protect the HVS, shall not cause any obstruction during monitoring;
    - j. permission must be obtained to set up the HVS and to obtain access to the monitoring stations; and
    - k. a secured supply of electricity is needed to operate the HVS.

**Construction Noise**

- 3.3.5 There were four (4) designated noise monitoring locations recommended in the Approved EM&A Manual Section 6.5.1.1. Based on rationale in Section 3.3.2, the Contract-related noise quality monitoring location for construction phase were summarized in **Table 3-3** and illustrated in **Appendix D**.

**Table 3-3 Designated Construction Noise Monitoring Location under the Project**

Location ID	Description in EM&A Manual	Location	Related Work Contract
CN-1	Village house to the west of Sha Ling Road	Village house to the west of Sha Ling Road (free field condition)	Contract 1
CN-2	Village house to the north of Man Kam To Road	Sha Ling Village House No. 25 (free field condition)	Contract 1 & 3
CN-3	Village house near San Uk Ling	San Uk Ling Village House No. 18 (free field condition)	Contract 2
CN-4	Village house of Muk Wu	Muk Wu Village House No. 267 (1m façade from the building)	Contract 2

**Water Quality**

3.3.6 There were four (4) water quality monitoring locations recommended in the Approved EM&A Manual Section 7.6.1.2. The locations and coordinates of water quality monitoring were listed in **Table 3-4**. Based on rationale in Section 3.3.2, the Contract-related water quality monitoring location for construction phase were summarized in **Table 3-4** and illustrated in **Appendix D**.

**Table 3-4 Designated Water Quality Monitoring Stations under the Project**

Proposed Location ID	Co-ordinates		Description	Related Work Contract
	North	East		
M1	843 431	831 308	Midstream of Nam Hang Stream	Contract 2
M2	843 840	831 101	Downstream of Nam Hang Stream	Contract 2
M3	843 509	830 040	Wetland in the Conservation Area near Yuen Leng Chai	Contract 1
M4	843 997	831 783	Watercourse across Lin Ma Hang Road, running from east of San Uk Ling to Man Kam To Boundary Control Point	Contract 2

**3.4 MONITORING FREQUENCY AND PERIOD**

3.4.1 The requirements of impact monitoring were stipulated in *Sections 5.8.1.1, 6.7.1.1 and 7.8.1.4* of the approved *EM&A Manual* and presented as follows.

**Air Quality Monitoring**

3.4.2 Monitoring frequency for air quality impact monitoring is as follows:

- 1-Hour TSP                      3 sets of 1-hour TSP monitoring shall be carried out once every six days during construction periods
- 24-Hour TSP                    24-hour TSP monitoring shall be carried out every six days during construction periods

**Noise Monitoring**

3.4.3 Noise impact monitoring shall be carried out once per week during construction periods. The noise measurement for the time period between 0700 and 1900 hours shall be measured in terms of  $L_{eq}$  (30 minutes) or 6 sets of  $L_{eq}$  (5mins).

**Water Quality Monitoring**

3.4.4 The monitoring frequency shall be 3 days per week during construction phase and the interval between two sets of monitoring shall not be less than 36 hours.

**3.5 MONITORING EQUIPMENT**

3.5.1 The monitoring equipment using for the EM&A program as proposed by the ET shall be verified by the IEC.

**Air Quality Monitoring**

3.5.2 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to IEC for approval.

3.5.3 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.

3.5.4 All equipment used by ET for air quality monitoring is listed in **Table 3-5**.

**Table 3-5 Air Quality Monitoring Equipment**

Equipment	Model
<b>24-hour TSP</b>	
High Volume Air Sampler (HVAS)	TISCH High Volume Air Sampler, HVS Model TE-5170
Calibration Kit	TISCH Model TE-5025A
<b>1-Hour TSP</b>	
Portable Dust Meter	Laser Dust Monitor, Model AM510

Equipment	Model
	/ Sibata LD-3 Laser Dust monitor Particle Mass Profiler & Counter

Wind Data Monitoring Equipment

- 3.5.5 According to the approved EM&A Manual, wind data monitoring equipment shall also be provided and set up for logging wind speed and wind direction near the dust monitoring locations. The equipment installation location shall be proposed by the ET and agreed with the IEC. For installation and operation of wind data monitoring equipment, the following points shall be observed:
- 1) The wind sensors should be installed 10 m above ground so that they are clear of obstructions or turbulence caused by buildings.
  - 2) The wind data should be captured by a data logger. The data shall be downloaded for analysis at least once a month.
  - 3) The wind data monitoring equipment should be re-calibrated at least once every six months.
  - 4) Wind direction should be divided into 16 sectors of 22.5 degrees each.
- 3.5.6 ET has liaised with the premises owners/ landlords to grant the permission for the HVS installation. However, they rejected to set up wind data monitoring equipment installation in their premises.
- 3.5.7 Under this situation, the ET proposed to obtain representative wind data from the Hong Kong Observatory Ta Kwu Ling Weather Station. Ta Kwu Ling Station is located near the Project site which situated at the sea level above 15mPD and the wind data monitoring equipment is installed 10 m above the existing ground.

Noise Monitoring

- 3.5.8 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in ms<sup>-1</sup> before each noise monitoring event. Noise measurements should not be made in fog, rain, wind with a steady speed exceeding 5 m s<sup>-1</sup> or wind with gusts exceeding 10 m s<sup>-1</sup>.
- 3.5.9 Noise monitoring equipment used for impact monitoring is listed in **Table 3-6**.

**Table 3-6 Noise Monitoring Equipment**

Equipment	Model
Integrating Sound Level Meter	Rion NL-52 Sound Level Meter /Rion NL-31 Sound Level Meter
Calibrator	Rion NC-73 Acoustical Calibrator
Portable Wind Speed Indicator	Testo Anemometer

- 3.5.10 Sound level meters listed above comply with the *International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1)* specifications, as recommended in TM issued under the NCO.

Water Quality Monitoring

- 3.5.11 Water quality parameters include dissolved oxygen, water temperature & depth, turbidity, salinity, pH and stream flow velocity shall be measured *in-situ*, and suspended solids shall be analyzed by a HOKLAS-accredited testing laboratory.

Dissolved Oxygen and Temperature Measurement

- 3.5.12 The dissolved oxygen (DO) measuring instruments should be portable and weatherproof. The equipment should also complete with cable and sensor, and DC power source. It should be capable of measuring:

- A DO level in the range of 0 – 20 mg/L and 0 – 200% saturation; and
- A temperature of 0 – 45 degree Celsius.

3.5.13 The equipment should have a membrane electrode with automatic temperature compensation complete with a cable.

3.5.14 Should salinity compensation not be built-in to the DO equipment, in-situ salinity should be measured to calibrate the DO measuring instruments prior to each measurement.

#### Turbidity Measurement

3.5.15 The turbidity measuring instruments should be a portable and weatherproof with DC power source. It should have a photoelectric sensor capable of measuring turbidity level between 0–1000 NTU (for example, Hach model 2100Q or an approved similar instrument).

#### Salinity Measurement

3.5.16 A portable salinometer capable of measuring salinity in the range of 0–40 parts per thousand (ppt) should be provided for measuring salinity of the water at each monitoring location.

#### pH Measurement

3.5.17 A portable pH meter capable of measuring a range between 0.0 and 14.0 should be provided to measure pH under the specified conditions accordingly to the APHA Standard Methods.

#### Water Depth Measurement

3.5.18 A portable, battery-operated echo sounder or an approved similar instrument should be used for water depths determination at each designated monitoring station.

#### Stream Flow Velocity Equipment

3.5.19 Since the EM&A Manuals do not specified instrument to use stream flow velocity measurement, the monitoring of stream flow velocity is therefore proposed to be conducted by using a flow probe which is a digital water velocity meter.

#### Water Sampling Equipment

3.5.20 A water sampler is required for suspended solid (SS) monitoring. A water sampler e.g. Kahlsico Water Sampler, which is a transparent PVC cylinder with capacity not less than 2 litres, will be used for water sampling if water depth over than 0.5m.

3.5.21 For sampling from very shallow water depths e.g. <0.5 m, water sample will be collected from water surface below 100mm using plastic bottle to avoid inclusion of bottom sediment or humus. Moreover, Teflon/stainless steel bailer or self-made sampling buckets maybe used for water sampling. The equipment used for sampling will be depended the sampling location and depth situations.

#### Sample Containers and Storage

3.5.22 Water samples for suspended solid should be stored in high density polythene bottles with no preservative added, packed in ice (cooled to 4°C without being frozen) and delivered to the laboratory within 24 hours of collection and be analyzed as soon as possible after collection.

3.5.23 Analysis of suspended solids should be carried out in a HOKLAS or other accredited laboratory. Water samples of about 1L should be collected at the monitoring stations for carrying out the laboratory suspended solids determination. The SS determination work should start within 24 hours after collection of the water samples. The SS analyses should follow the *APHA Standard Methods 2540D* with Limit of Reporting of 2 mg/L.

3.5.24 Details of the equipment used for water quality monitoring are listed in **Table 3-7** below.

**Table 3-7 Water Quality Monitoring Equipment**

Equipment	Model
Water Depth Detector	Tape measures
Water Sampler	A 2-litre transparent PVC cylinder with latex cups at both ends or Teflon/stainless steel bailer or self-made sampling bucket
Thermometer & DO meter	YSI Professional DSS
pH meter	YSI Professional DSS
Turbidimeter	YSI Professional DSS
Salinometer	YSI Professional DSS
Stream Flow Velocity	FP211 Global Flow Probe
Sample Container	High density polythene bottles (provided by laboratory)
Storage Container	'Willow' 33-litter plastic cool box with Ice pad

3.5.25 Furthermore, Suspended Solids (SS) analysis was carried out by *ALS Technichem (HK) Pty Ltd.* Which is one a local HOKLAS-accredited laboratory

### 3.6 EQUIPMENT CALIBRATION

- 3.6.1 The HVAS is operated and calibrated on a regular basis in accordance with the manufacturer's instruction using Tisch Calibration Kit Model TE-5025A. Calibration would carry out at fortnightly interval. The calibration data are properly documented and the records are maintained by ET for future reference. Furthermore, Tisch Calibration Kit will be calibrated by the manufacturer in yearly basis.
- 3.6.2 The 1-hour TSP meter calibrated by a local HOKLAS-accredited laboratory would be undertaken in yearly basis. Zero response of the equipment was checked before and after each monitoring event.
- 3.6.3 The sound level meter and acoustic calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis.
- 3.6.4 The multi-parameter Water Quality Monitoring System is calibrated by HOKLAS accredited laboratory of three month intervals.
- 3.6.5 All updated calibration certificates of the monitoring equipment used for the impact monitoring program in this Reporting Month are attached in [Appendix E](#).

### 3.7 DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.7.1 The impact monitoring data are handled by the ET's systematic data recording and management, which complies with in-house Quality Management System. Standard Field Data Sheets (FDS) are used in the impact monitoring program.
- 3.7.2 The monitoring data recorded in the equipment e.g. 1-hour TSP meter, noise meter and Multi-parameter Water Quality Monitoring System are downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data are input into a computerized database properly maintained by the ET. The laboratory results are input directly into the computerized database and QA/QC checked by personnel other than those who input the data. For monitoring activities require laboratory analysis, the local laboratory follows the QA/QC requirements as set out under the HOKLAS scheme for all laboratory testing.

### 3.8 DETERMINATION OF ACTION/LIMIT (A/L) LEVELS

- 3.8.1 The baseline monitoring results form the basis for determining the environmental acceptance criteria for the impact monitoring. The air quality, construction noise and water quality criteria, namely Action and Limit levels were established according to Approved EM&A Manual, and they are listed in *Tables 3-8, 3-9* and *3-10* below.

**Table 3-8 Action and Limit Levels for Air Quality Monitoring**

Monitoring Station	Action Level ( $\mu\text{g}/\text{m}^3$ )		Limit Level ( $\mu\text{g}/\text{m}^3$ )	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP

Monitoring Station	Action Level ( $\mu\text{g}/\text{m}^3$ )		Limit Level ( $\mu\text{g}/\text{m}^3$ )	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
ASR-1	331	181	500	260
ASR-2	316	165	500	260
ASR-3	307	160	500	260

**Table 3-9 Action and Limit Levels for Construction Noise**

Monitoring Location	Action Level	Limit Level in dB(A)
	Time Period: 0700-1900 hours on normal weekdays	
CN-1,CN-2, CN-3, CN-4	When one or more documented complaints are received	75 dB(A)

Note: \* Reduces to 70 dB(A) for schools and 65 dB(A) during the school examination periods.

**Table 3-10 Action and Limit Levels for Water Quality**

Parameter	Performance criteria	Monitoring Location			
		M1	M2	M3	M4
DO (mg/L)	Action Level	3.03	4.99	4.58	3.62
	Limit Level	2.97	4.90	4.49	3.52
Turbidity (NTU)	Action Level	7.1	39.7	5.6	5.4
	Limit Level	7.6	42.2	5.9	5.9
SS (mg/L)	Action Level	8.5	29.0	9.3	4.8
	Limit Level	10.1	31.0	9.5	5.0

Notes:

- For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits
- For turbidity and SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

3.8.2 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan enclosed in [Appendix F](#).

#### 4. AIR QUALITY

##### 4.1 MONITORING RESULTS

4.1.1 In the Reporting Month, air quality monitoring was performed at all designated locations. Impact monitoring schedule provided to all relevant parties was shown in [Appendix G](#).

4.1.2 In this Reporting Month, there were 5 sessions of 24-hour TSP and 12 sessions of 1-hour TSP undertaken at each designated station for air quality monitoring. The air quality monitoring results are summarized in [Tables 4-1 to 4-3](#). The database of 24-hour TSP is shown in [Appendix H](#) and the graphical plots of monitoring result are shown in [Appendix I](#).

**Table 4-1 Summary of Air Quality Monitoring Results at ASR-1 under Contract 1**

Date	24-hour TSP (µg/m <sup>3</sup> )	1-hour TSP (µg/m <sup>3</sup> )				
		Date	Start Time	1 <sup>st</sup> hour measured	2 <sup>nd</sup> hour measured	3 <sup>rd</sup> hour measured
2 Feb 23	63	6-Feb-23	13:00	68	77	70
8 Feb 23	34	11-Feb-23	13:00	91	89	93
14 Feb 23	39	17-Feb-23	9:26	90	87	88
20 Feb 23	31	23-Feb-23	13:00	93	89	92
25 Feb 23	72					
Average (Range)	<b>48</b> (31 – 72)	Average (Range)		<b>86</b> (68 – 93)		

**Table 4-2 Summary of Air Quality Monitoring Results at ASR-2 under Contract 2**

Date	24-hour TSP (µg/m <sup>3</sup> )	1-hour TSP (µg/m <sup>3</sup> )				
		Date	Start Time	1 <sup>st</sup> hour measured	2 <sup>nd</sup> hour measured	3 <sup>rd</sup> hour measured
2 Feb 23	129	6-Feb-23	13:08	82	87	81
8 Feb 23	54	11-Feb-23	13:06	91	93	89
14 Feb 23	40	17-Feb-23	9:57	88	91	90
20 Feb 23	41	23-Feb-23	13:05	89	93	91
25 Feb 23	133					
Average (Range)	<b>80</b> (40 – 133)	Average (Range)		<b>89</b> (81 – 93)		

**Table 4-3 Summary of Air Quality Monitoring Results at ASR-3a under Contract 2**

Date	24-hour TSP (µg/m <sup>3</sup> )	1-hour TSP (µg/m <sup>3</sup> )				
		Date	Start Time	1 <sup>st</sup> hour measured	2 <sup>nd</sup> hour measured	3 <sup>rd</sup> hour measured
2 Feb 23	49	6-Feb-23	13:12	75	72	76
8 Feb 23	117	11-Feb-23	13:12	88	90	87
14 Feb 23	18	17-Feb-23	13:06	86	85	89
20 Feb 23	43	23-Feb-23	13:16	87	89	90
25 Feb 23	22					
Average (Range)	<b>50</b> (22 – 117)	Average (Range)		<b>85</b> (72 – 90)		

##### 4.2 AIR MONITORING EXCEEDANCE

4.2.1 As shown in [Tables 4-1 to 4-3](#), the monitoring results of 24-hour and 1-hour TSP monitoring in the Reporting Month were below the Action/ Limit Level. No Notification of Exceedance (NOE) of air quality monitoring criteria was issued and therefore corrective action was not required. The meteorological data during the impact monitoring days are summarized in [Appendix J](#).

## 5. CONSTRUCTION NOISE

### 5.1 MONITORING RESULTS

- 5.1.1 In the Reporting Month, noise monitoring was performed at all designated locations. Impact monitoring schedule provided to all relevant parties was shown in [Appendix G](#).
- 5.1.2 In this Reporting Month, **3** sessions of noise monitoring were undertaken at each designated noise monitoring location. The sound level were set in a free field situation for CN1, CN2 and CN3 and therefore a façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines. The monitoring result of noise monitoring is show in [Tables 5-1 and 5-2](#) and the graphical plots are shown in [Appendix I](#).

**Table 5-1 Summary of Construction Noise Monitoring Results under Contract 1**

Construction Noise Level ( $L_{eq30min}$ ), dB(A)				
Date	Start Time	CN1(*)	Start Time	CN2(*)
6 Feb 23	13:02	66	13:36	66
17 Feb 23	14:05	66	10:48	60
23 Feb 23	13:00	65	13:35	60
<b>Limit Level</b>	<b>75 dB(A)</b>			

(\*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

**Table 5-2 Summary of Construction Noise Monitoring Results under Contract 2**

Construction Noise Level ( $L_{eq30min}$ ), dB(A)				
Date	Start Time	CN3(*)	Start Time	CN4
6 Feb 23	14:10	61	14:43	63
17 Feb 23	9:58	63	13:10	61
23 Feb 23	14:09	64	14:48	62
<b>Limit Level</b>	<b>75 dB(A)</b>			

(\*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

- 5.1.3 Prior and after noise monitoring, the accuracy of the sound level meter has been checked by an acoustic calibrator to ensure the measurement within acceptance range of  $\pm 0.5$ dB. Moreover, wind speed checked by portable wind speed meter has been performed before noise monitoring. No noise measurement was performed in fog, rain, wind with a steady speed exceeding  $5 \text{ m s}^{-1}$  or wind with gusts exceeding  $10 \text{ m s}^{-1}$ .

### 5.2 NOISE MONITORING EXCEEDANCE

- 5.2.1 As shown in [Tables 5-1 and 5-2](#), no noise complaint (which triggered Action Level) and Limit Level exceedance for noise monitoring exceedance was recorded in the Reporting Month.



## 6. WATER QUALITY

### 6.1 MONITORING RESULTS

6.1.1 In the Reporting Month, water quality monitoring was performed at all designated locations. Impact monitoring schedule provided to all relevant parties was shown in [Appendix G](#).

6.1.2 In the Reporting Month, a total of **12** monitoring days were carried out for water quality impact monitoring. The monitoring result of key parameters including Dissolved Oxygen, Turbidity and Suspended Solids are summarized in [Tables 6-1](#) and [6-2](#). Detailed monitoring results including in-situ measurements and laboratory analysis data are shown in [Appendix H](#) and graphical plots for monitoring result are shown in [Appendix I](#).

**Table 6-1 Summary of Water Quality Monitoring Results – M3 under Contract 1**

Date	Parameters		
	DO (Averaged) (mg/L)	Turbidity (Averaged) (NTU)	Suspended Solids (Averaged) (mg/L)
1 Feb 23	8.68	0.7	4.0
3 Feb 23	8.50	0.1	4.0
6 Feb 23	8.36	1.8	2.5
8 Feb 23	8.38	2.1	2.5
10 Feb 23	8.29	1.2	2.5
13 Feb 23	8.23	0.4	<2
15 Feb 23	8.24	2.4	2.5
17 Feb 23	8.18	1.7	2.0
20 Feb 23	9.08	1.8	3.0
22 Feb 23	9.22	1.0	5.5
24 Feb 23	9.00	0.6	<2
27 Feb 23	8.90	1.3	2.0

**Table 6-2 Summary of Water Quality Monitoring Results (M1, M2 and M4) under Contract 2**

Date	Parameters								
	DO (Averaged) (mg/L)			Turbidity (Averaged) (NTU)			Suspended Solids (Averaged) (mg/L)		
	M1	M2	M4	M1	M2	M4	M1	M2	M4
1 Feb 23	8.80	8.84	8.78	1.3	0.5	3.7	6.5	<2	4.0
3 Feb 23	8.81	8.63	8.57	1.1	0.4	3.5	<2	<2	4.0
6 Feb 23	8.60	8.54	8.37	1.8	3.4	1.6	<2	<2	<2
8 Feb 23	8.48	8.61	8.21	1.0	2.5	1.9	<2	2.0	4.5
10 Feb 23	8.46	8.60	8.17	1.4	6.7	1.6	<2	<2	<2
13 Feb 23	8.28	8.23	8.24	1.1	1.5	1.4	<2	3.5	<2
15 Feb 23	8.34	8.39	8.29	1.0	3.6	2.3	4.5	<2	2.5
17 Feb 23	8.37	8.20	8.40	1.2	1.1	2.3	<2	4.0	4.5
20 Feb 23	9.20	10.26	8.57	0.2	1.3	1.7	6.5	6.5	2.5
22 Feb 23	10.21	9.79	9.01	2.0	1.7	0.4	5.0	3.5	2.0
24 Feb 23	8.62	8.93	8.37	3.2	1.4	0.1	<2	3.5	2.5
27 Feb 23	8.41	9.03	8.33	1.6	0.7	0.4	5.5	<2	2.5

6.1.3 During the Reporting Month, field measurements including temperature of stream water, salinity concentrations, pH values and the stream flow velocity for all monitoring locations are summarized in [Table 6-3](#).

**Table 6-3 Summary of Field Measurements for Water Quality**

Monitoring Location	Parameters of field measurements							
	pH (Averaged) (unit)		Salinity (Averaged) (ppt)		Temp (Averaged) (°C)		Water Flow (Averaged) (m/s)	
	min	max	min	max	min	max	min	max
M1	7.2	8.7	0.03	0.05	16.1	19.6	<0.1	<0.1
M2	7.0	8.2	0.04	0.11	16.7	21.5	<0.1	<0.1
M3	7.1	8.3	0.01	0.09	17.0	21.5	<0.1	<0.1
M4	7.0	8.3	0.04	0.09	16.9	20.1	<0.1	<0.1

**6.2 WATER QUALITY MONITORING EXCEEDANCE**

6.2.1 In this Reporting Month, no water quality exceedances were recorded. The summary of non-compliance of water quality performance is shown in [Table 6-4](#).

**Table 6-4 Action and Limit (A/L) Levels Exceedance Record**

Station	DO		Turbidity		SS		Total Exceedance		Project Related exceedance	
	Action	Limit	Action	Limit	Action	Limit	Action	Limit	Action	Limit
M1	0	0	0	0	0	0	0	0	0	0
M2	0	0	0	0	0	0	0	0	0	0
M3	0	0	0	0	0	0	0	0	0	0
M4	0	0	0	0	0	0	0	0	0	0

6.2.1 Notification of Exceedance and the investigation for exceedance in the Reporting Month is summarized in [Table 6-5](#).

**Table 6-5 Summary of Investigation of Water Quality Exceedance in the Reporting Month**

Date of Exceedance	Exceeded Location	Exceeded Parameter	Cause of Water Quality Exceedance
--	--	--	--

## 7. ECOLOGY MONITORING

### 7.1 REQUIREMENT

- 7.1.1 According to approved EIA report (AEIAR-198/2016), habitat types within project boundary comprise of watercourse, grassland, upland grassland, plantation, woodland and developed area. Natural habitats were of moderate ecological value in terms of species diversity, species rarity, species abundance, ecological linkage as well as nursery. Moreover, 0.3ha of wet woodland on the northern side of Sandy Ridge was deemed habitat with high ecological value. Four types of habitats were regarded as ecologically sensitive habitats, namely wet woodland, watercourses, upland grassland and woodland. Considering human disturbance in upcoming construction and operation phases, ecologically sensitive habitats shall be monitored in accordance with EM&A Manual.
- 7.1.2 The objective of ecologically sensitive habitats monitoring is to evaluate the effectiveness of measures to minimize impacts on concerned habitats from disturbance and pollution. In order to monitor the effectiveness of the measures to the minimize impact on ecologically sensitive habitats from disturbance and pollution, monthly monitoring during construction and operation phases is required as specified in EM&A Manual. Standard faunal transect and sampling surveys cover both wetland habitats (*wet woodland and watercourse*) and non-wetland habitats (*upland grassland and woodland*).

### 7.2 METHODOLOGY

- 7.2.1 Wetland habitats include wet woodland and watercourses. Monitoring surveys using standardized quantitative methodology will conduct at fixed points. For seasonal watercourse, the survey will be conducted whenever the habitat appears. Measures to respond to decreases in numbers of aquatic fauna using the wetland habitats and Action/Limit levels to trigger these measures are detailed in **Table 7-1**.

**Table 7-1 Action and Limit Levels for Wet Woodland Habitats Monitoring**

Action Level	Response	Limit Level	Response
Reduction in taxa diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in taxa diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

*Remarks: Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna*

- 7.2.2 Non-wetland habitats consist of upland grassland and woodland. Monthly quantitative surveys of non-aquatic fauna will be conducted using standard route transect counts. Measures to respond to decreases in numbers of non-aquatic fauna using the non-wetland habitats and Action/Limit levels to trigger these measures are detailed in **Table 7-2**.

**Table 7-2 Action and Limit Levels for Non-Wet Woodland Habitats Monitoring**

Action Level	Response	Limit Level	Response
Reduction in species diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in species diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

*Remarks: Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna*

- 7.2.3 The ecological survey includes all taxa being investigated in accordance with EIA report. Schedule of faunal surveys in each year during construction phase is presented in **Table 7-3**.

**Table 7-3 Schedule of Faunal Surveys in each year During Construction Phase**

Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Mammals	√	√	√	√	√	√	√	√	√	√	√	√
Birds (day)	√	√	√	√	√	√	√	√	√	√	√	√

Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Birds (night)				√	√	√	√	√	√	√		
Herpetofauna				√	√	√	√	√	√	√		
Dragonflies			√	√	√	√	√	√	√	√		
Butterflies			√	√	√	√	√	√	√	√		
Aquatic fauna	√	√	√	√	√	√	√	√	√	√	√	√

Mammal Survey

7.2.4 Mammal surveys will be conducted along the proposed transects (shown in **Appendix K** - Ecological Survey Reports) in during both daytime and night time periods. Along with direct observations, other field signs, such as scats and tracks, will be searched and recorded if present.

Bird Survey

7.2.5 Bird surveys will be conducted along the transects (shown in **Appendix K** - Ecological Survey Reports) during the surveys, species and their vocalizing individuals recorded will be enumerated and recorded according to the habitat(s) they are utilizing.

Herpetofauna Survey

7.2.6 Reptile and amphibian surveys will be conducted along transects (shown in **Appendix K** - Ecological Survey Reports) during surveys careful searches of appropriate microhabitats and refugia for reptiles and their vocalizing individuals will be undertaken and all reptiles observed will be identified and counted.

Dragonfly and Butterfly Survey

7.2.7 Dragonfly and Butterfly surveys will be conducted along transects (shown in **Appendix K** - Ecological Survey Reports) during surveys all dragonflies and Butterflies seen will be identified and counted as accurately as possible.

Aquatic Fauna Survey

7.2.8 Freshwater fishes and macro-invertebrates will be recorded by direct observation. All species trapped/recorded will be enumerated and identified (to the lowest taxonomic level possible), and the species of conservation importance photographed.

7.2.9 After each ecological monitoring survey, a monthly report of the survey result and data collected will be provided with reference to EM&A Manual. An annual analysis of data will be carried out in order to study if there is any significant reduction in taxa diversity and abundance.

**7.3 ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 1)**

7.3.1 In the Reporting Month, ecological monitoring was undertaken on **11<sup>th</sup> February 2023**, a sunny day. The day survey covered wetland and non-wetland areas. The survey was conducted by transect and at fixed points. All species seen would be identified and counted as accurately as possible. Results of the monitoring survey are presented below:

Monitoring Result for Contract 1

Mammal

7.3.2 There was no mammal species recorded in the monitoring area.

Birds

7.3.3 There were a total of 27 bird individuals from 8 species recorded in the monitoring area. No Golden-headed Cisticola was observed during the bird survey.

Herpetofauna

7.3.4 There was no reptile species recorded in monitoring area. There was no amphibian species recorded in the monitoring area.

Butterfly

7.3.5 There were a total of 4 butterfly individuals from 2 species recorded in the monitoring area.

Dragonfly

7.3.6 There was no odonate recorded in the monitoring area.

Aquatic Fauna Survey (Freshwater communities)

7.3.7 There was no freshwater community recorded in the monitoring area.

7.3.8 The summaries of faunal survey result are shown in **Tables 7-4** and **7-5**.

**Table 7-4 Result of Faunal Survey under Contract 1**

Scientific Name	Common / Engineer Name	Chinese Name	Conservation Status	Non-wetland		Wetland		
				UG	WL	MA	WW	WC
<b>Mammal Survey</b>								
--	--	--	--	--	--	--	--	--
<b>Avifauna Survey</b>								
<i>Spilopelia chinensis</i>	Spotted Dove	珠頸斑鳩					2	
<i>Pycnonotus jocosus</i>	Red-whiskered Bulbul	紅耳鶇					7	
<i>Phylloscopus fuscatus</i>	Dusky Warbler	褐柳鶇					2	
<i>Phylloscopus inornatus</i>	Yellow-browed Warbler	黃眉柳鶇		2				
<i>Prinia flaviventris</i>	Yellow-bellied Prinia	黃腹鷓鴣		1			2	
<i>Orthotomus sutorius</i>	Common Tailorbird	長尾縫葉鶇		3				
<i>Garrulax perspicillatus</i>	Masked Laughingthrush	黑臉噪鶇					7	
<i>Phoenicurus aureus</i>	Davaian Redstart	北紅尾鶇					1	
<b>Reptile Survey</b>								
N/A	--	--	--	--	--	--	--	--
<b>Amphibian Survey</b>								
N/A	--	--	--	--	--	--	--	--
<b>Butterfly Survey</b>								
<i>Mycalesis mineus</i>	Dark Brand Bush Brown	小眉眼蝶					2	
<i>Abisara echerius</i>	Plum Judy	蛇目褐蛺蝶		2				
<b>Odonate Survey</b>								
N/A	--	--	--	--	--	--	--	--

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 7-5 Result of Freshwater Communities Survey under Contract 1**

Scientific Name	Common Name	Chinese Name	Conservation Status	Non-wetland		Wetland		
				UG	WL	MA	WW	WC
N/A	--	--	--	--	--	--	--	--

Discussion

7.3.9 After analysing survey results in February from 2019 to 2023, there was no significant drop in species richness and abundance for wetland habitat. Yet, good site practice during construction, with reference to EM&A Manual, is required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. In addition, implementing proper waste disposal is necessary to reduce contamination to water and soil. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.

**7.4 ECOLOGICAL MONITORING SURVEY FINDINGS (CONTRACT 2)**

7.4.1 In the Reporting Month, ecological monitoring was undertaken at work area of Contract 2 on **11<sup>th</sup> February 2023**, a sunny day. The day and night survey covered wetland and non-wetland areas. The survey was conducted by transect and at fixed point. All species seen would be identified and counted as accurately as possible. Results of the monitoring survey are presented below:

**Monitoring Result for Contract 2**

**Mammal**

7.4.2 There was no mammal recorded in the monitoring area

**Birds**

7.4.3 There were a total of 4 bird individuals from 3 species recorded in the monitoring area. No Golden-headed Cisticola was observed during the bird survey.

**Herpetofauna**

7.4.4 There was no reptile recorded in the monitoring area. There was no amphibian recorded in the monitoring area.

**Butterfly**

7.4.5 There was no butterfly individual recorded in the monitoring area.

**Dragonfly**

7.4.6 There was no odonate individual recorded in the monitoring area.

**Aquatic Fauna Survey (Freshwater communities)**

7.4.7 There were 2 species of freshwater fish were recorded in the monitoring area.

7.4.8 The summaries of faunal survey result are shown in **Tables 7-6** and **7-7**.

**Table 7-6 Result of Faunal Survey under Contract 2**

Scientific Name	Common / Engineer Name	Chinese Name	Conservation Status	Non-wetland		Wetland		
				UG	WL	MA	WW	WC
<b>Mammal Survey</b>								
--	--	--	--	--	--	--	--	--
<b>Avifauna Survey</b>								
<i>Amaurornis phoenicurus</i>	White-breasted Waterhen	白胸苦惡鳥				1		
<i>Prinia flaviventris</i>	Yellow-bellied Prinia	黃腹鷦鶯		2				
<i>Orthotomus sutorius</i>	Common Tailorbird	長尾縫葉鶯		1				
<b>Reptile Survey</b>								
--	--	--	--	--	--	--	--	--
<b>Amphibian Survey</b>								
--	--	--	--	--	--	--	--	--
<b>Butterfly Survey</b>								
--	--	--	--	--	--	--	--	--
<b>Odonate Survey</b>								
--	--	--	--	--	--	--	--	--

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 7-7 Result of Freshwater Communities Survey under Contract 2**

Scientific Name	Common Name	Chinese Name	Conservation Status	Non-wetland		Wetland		
				UG	WL	MA	WW	WC
<i>Gambusia affinis</i>	Mosquito fish	食蚊魚						+
<i>Puntius</i>	Chinese Barb	五線無鬚魮						+

Scientific Name	Common Name	Chinese Name	Conservation Status	Non-wetland		Wetland		
				UG	WL	MA	WW	WC
<i>semifasciolatus</i>								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

+: Species appeared but uncountable.

**Discussion**

- 7.4.9 After analysing survey results in February 2019 to 2023, there was a decrease in species richness and abundance for wetland and non-wetland habitats. Still, a good site practice during construction, with reference to EM&A Manual, is still required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. In addition, implementing proper waste disposal is necessary to reduce contamination to water and soil. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.
- 7.4.10 The detailed Ecological Survey Reports for Contract 1 and Contract 2 are attached in **Appendix K**.
- 7.4.11 The tentative ecology inspection and monitoring in the next Reporting Month (March 2023) is scheduled on **13<sup>th</sup> March 2023**.

**7.5 MONITORING OF FLORA SPECIES OF CONSERVATION INTEREST UNDER CONTRACT 1**

- 7.5.1 According to the approved vegetation survey report and transplantation proposal under FEP-01/534/2017/A, an individual of flora species of conservation interest (the transplanted T-2928) was identified and transplanted to the receptor site.
- 7.5.2 According to approved vegetation survey report and transplantation proposal, post-transplantation monitoring was conducted once per week in the first three months after the transplantation in Oct 2018 and once in each of the following month in the remaining establishment period for 12 month. During the remaining construction phase of the project, the transplanted T-2928 would be monitored on quarterly basis.
- 7.5.3 A landscape sub-contractor was employed by the Contractor to monitor the health condition of transplanted species and provide advice on necessary weeding, fertilizing and pest control. The monitoring records were submitted to ET and IEC for review and record. Moreover, inspection of the transplanted T-2928 was undertaken by ET as part of the weekly site inspection. No construction activity and disturbance were observed at the location of the transplanted T-2928. The health condition of the transplanted T-2928 was fair with normal foliage color and density.

**7.6 MEASURE FOR PROTECTION OF NESTING BIRD**

- 7.6.1 Pursuant to FEP-01/534/2017/A condition 2.19 and EP-534/2017/A condition 2.20, precautionary checks for the presence of nesting birds shall be carried out in the breeding season (February to July) before vegetation clearance.
- 7.6.2 In the Reporting Period, there was no vegetation clearance for both Contract 1 and Contract 2, and precautionary check for the presence of nesting birds was not required to carry out.

## 8. LANDSCAPE AND VISUAL

### 8.1 REQUIREMENT

- 8.1.1 The EIA has recommended EM&A for landscape and visual resources to be undertaken during the design, construction and operational stages of the project. The design, implementation and maintenance of landscape mitigation measures is a key aspect of this and should be checked to ensure that they are fully realized and that potential conflicts between the proposed landscape measures and any other project works let its are resolved at the earliest possible date and without compromise to the intention of the mitigation measures. In addition, implementation of the mitigation measures recommended by the EIA will be monitored through the site audit programme.
- 8.1.2 A number of mitigation measures to ameliorate the landscape and visual impacts of the Project implementation is summarized in the EMIS of *Appendix 13.1* of the EIA Report.
- 8.1.3 The landscape and visual mitigation measures proposed should be incorporated in the landscape and engineering design. Mitigation measures to be implemented during construction should be adopted from the start of construction and be in place throughout the entire construction period. Mitigation measures to be implemented during operation should be integrated into the detailed design and built as part of the construction works so that they are in place on commissioning of the Project. Tree transplantation and compensatory planting should be carried out as early as possible in the Project with transplantation carried out prior to construction starting in any particular area.
- 8.1.4 During construction phase, Landscape & Visual Monitoring of the contractor’s operations should be conducted monthly and reported by ET, and countersigned by IEC.

### 8.2 FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH

- 8.2.1 In the Reporting Month, landscape & visual inspection was carried out by the Registered Landscape Architect for works area of Contract 1 and Contract 2 on *28<sup>th</sup> February 2023*. The findings / reminders recorded during the inspection are presented in *Tables 8-1 and 8-2*.

**Table 8-1 Landscape & Visual Inspection Finding for Contract 1**

Date	Findings and Reminder	Follow-Up Status
28 <sup>th</sup> February 2023	1. The Contractor is reminded to set up TPZ of proper size and with appropriate material around retain trees according to approved method statement.	• Reminded only
	2. The Contractor is reminded to prevent the construction material pile within TPZ and ensure no works is allowed within the TPZ.	• Reminder only
	3. Transplanted tree T2465 and T2928 were in fair health condition with normal foliage color and density. Contractor is reminded to provide proper maintenance according to the method statement.	• Reminder only

**Table 8-2 Landscape & Visual Inspection Finding for Contract 2**

Date	Findings and Reminder	Follow-Up Status
28 <sup>th</sup> February 2023	1. Contractor is reminded to set up TPZ of proper size and with appropriate material around retain trees according to approved method statement. Contractor should prevent any construction material pile within TPZ and ensure no works is allowed within the TPZ.	• Reminder only

- 8.2.2 Inspection checklist of Landscape & Visual signed by RLA is attached in *Appendix L*.



## 9. WASTE MANAGEMENT

### 9.1 GENERAL WASTE MANAGEMENT

9.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time in accordance with the Waste Management Plan (WMP).

### 9.2 RECORDS OF WASTE QUANTITIES

9.2.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

9.2.2 The quantities of waste for disposal in this Reporting Month are summarized in [Table 9-1](#) and [9-2](#) and the Monthly Summary Waste Flow Table is shown in [Appendix M](#). Whenever possible, materials were reused on-site as far as practicable.

**Table 9-1 Summary of Quantities of Inert C&D Materials**

Type of Waste	Contract 1		Contract 2	
	Quantity	Disposal Location	Quantity	Disposal Location
Total generated C&D Materials (Inert) ('000m <sup>3</sup> )	0.300	--	356.600 (#)	--
Reused in this Contract (Inert) ('000m <sup>3</sup> )	0	--	0	--
Reused in other Projects (Inert) ('000m <sup>3</sup> )	0	--	0	--
Disposal as Public Fill (Inert) ('000m <sup>3</sup> )	0.300	Tuen Mun Area 38	356.600 (#)	Tuen Mun Area 38

Remark: the unit is '000kg

**Table 9-2 Summary of Quantities of C&D Wastes**

Type of Waste	Contract 1		Contract 2	
	Quantity	Disposal Location	Quantity	Disposal Location
Recycled Metal ('000kg)	0	--	0	--
Recycled Paper / Cardboard Packing ('000kg)	0	--	0	--
Recycled Plastic ('000kg)	0	--	0	--
Chemical Wastes ('000kg)	0	--	0	--
General Refuses ('000m <sup>3</sup> )	0.015	NENT Landfill	9.000 (#)	NENT Landfill

Remark: (#) the unit is in '000kg

9.2.3 Since canteen and/or kitchen are not allowed setting on the Project site, no domestic wastewater was generated from the Project.

## 10. SITE INSPECTION

### 10.1 REQUIREMENT

10.1.1 According to the approved EM&A Manual, environmental site inspection should be led by RE and attended by the Contractor and ET at least once per week. Regular environmental site inspections shall be carried out to assess the environmental performance.

### 10.2 FINDINGS / DEFICIENCIES DURING SITE INSPECTION IN THE REPORTING MONTH

#### Contract 1

10.2.1 In the Reporting Month, joint site inspections for Contract 1 to evaluate the site environmental performance were carried out by the RE, ET and the Contractor on **2<sup>nd</sup>, 9<sup>th</sup>, 16<sup>th</sup>, and 23<sup>rd</sup> February 2023** and IEC attended joint site inspection on **16<sup>th</sup> February 2023**. No non-compliance was noted in the Reporting Month. The findings / deficiencies that observed during the weekly site inspection are listed in **Table 10-1**.

**Table 10-1 Site Observations for the Works of Contract 1**

Date	Findings / Deficiencies	Follow-Up Status
2 <sup>nd</sup> February 2023	• The Contactor was reminded to spray water at exposed area regularly to minimise fugitive dust.	Reminder only.
9 <sup>th</sup> February 2023	• No adverse environmental issue was observed.	N/A
16 <sup>th</sup> February 2023	• White smoke was observed, the Contractor was reminded to provide maintenance for the plant regularly.	Reminder only.
23 <sup>rd</sup> February 2023	• No adverse environmental issue was observed.	N/A

#### Contract 2

10.2.2 In the Reporting Month, joint site inspections for Contract 2 to evaluate the site environmental performance carried out by the RE, ET and the Contractor was on **2<sup>nd</sup>, 9<sup>th</sup>, 16<sup>th</sup>, and 23<sup>rd</sup> February 2023** and IEC attended joint site inspection on **16<sup>th</sup> February 2023**. No non-compliance was noted in the Reporting Month. The findings / deficiencies that observed during the weekly site inspection are listed in **Table 10-2**.

**Table 10-2 Site Observations for the Works of Contract 2**

Date	Findings / Deficiencies	Follow-Up Status
2 <sup>nd</sup> February 2023	• No adverse environmental issue was observed.	N/A
9 <sup>th</sup> February 2023	• No adverse environmental issue was observed.	N/A
16 <sup>th</sup> February 2023	• No adverse environmental issue was observed.	N/A
23 <sup>rd</sup> February 2023	• No adverse environmental issue was observed.	N/A

## 11. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

### 11.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

11.1.1 In the Reporting Month, no environmental complaint was received for the project. No summons and prosecution was lodged for the Contract. The statistical summary table of the environmental complaint, summons and prosecution are presented in *Tables 11-1, 11-2* and *11-3*. The complaint log for the Project is shown in *Appendix N*.

**Table 11-1 Statistical Summary of Environmental Complaints**

Reporting Month		Environmental Complaint Statistics		
		Frequency	Cumulative	Complaint Nature
1 <sup>st</sup> – 28 <sup>th</sup> February 2023	Contract 1	0	2	(1) Air Quality (1) Noise
1 <sup>st</sup> – 28 <sup>th</sup> February 2023	Contract 2	0	5	(1) Water (2) Air Quality (1) Noise (1) Soil / muddy water

**Table 11-2 Statistical Summary of Environmental Summons**

Reporting Month		Environmental Summons Statistics		
		Frequency	Cumulative	Complaint Nature
1 <sup>st</sup> – 28 <sup>th</sup> February 2023	Contract 1	0	0	NA
1 <sup>st</sup> – 28 <sup>th</sup> February 2023	Contract 2	0	0	NA

**Table 11-3 Statistical Summary of Environmental Prosecution**

Reporting Month		Environmental Prosecution Statistics		
		Frequency	Cumulative	Complaint Nature
1 <sup>st</sup> – 28 <sup>th</sup> February 2023	Contract 1	0	0	NA
1 <sup>st</sup> – 28 <sup>th</sup> February 2023	Contract 2	0	0	NA

11.1.2 In addition, no complaints received and emergency event relating to violation of environmental legislation for illegal dumping and landfilling were received.

## 12. IMPLEMENTATION STATUS OF MITIGATION MEASURES

### 12.1 GENERAL REQUIREMENTS

12.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the approved EM&A Manual covered the issues of dust, noise, water and waste.

12.1.2 The Works of Contract 1 and Contract 2 under the Project shall be implementing the required environmental mitigation measures according to the approved EM&A Manual subject to the site condition. Environmental mitigation measures implemented in this Reporting Month is summarized in **Table 12-1**. The status of the Environmental mitigation measures are presented in **Appendix O**.

**Table 12-1 Environmental Mitigation Measures**

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> <li>• Provided efficient silt removal facilities to reduce SS level before effluent discharge.</li> <li>• Provided ditches, earth bunds or sand bag barriers to minimize polluted runoff.</li> <li>• Temporary drainage was provided to prevent runoff going through site surface and minimize polluted runoff.</li> <li>• Provided perimeter cut-off drains at site boundaries to intercept storm runoff from crossing the site.</li> <li>• Exposed slopes surface were compacted and covered with tarpaulin or similar means.</li> <li>• Provided portable chemical toilets on site.</li> </ul>
Air Quality	<ul style="list-style-type: none"> <li>• Maintain damp / wet surface on access road.</li> <li>• Maintain low vehicular speed within the works areas.</li> <li>• Provided vehicle wheel washing facilities at each construction site exit;</li> <li>• Provided water spraying every hour for all active works area.</li> <li>• Stockpiles of dusty material were covered with impervious sheeting.</li> <li>• Provided workers to clear dusty materials at the vehicle entrance or exit regularly.</li> <li>• Stockpile more than 20 bags of cement or dry pulverized fuel ash (PFA) has been covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.</li> </ul>
Noise	<ul style="list-style-type: none"> <li>• Restricted operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday.</li> <li>• Keep good maintenance of plants.</li> <li>• Placed noisy plants away from residence and school.</li> <li>• Provided noise barriers or hoarding to enclose the noisy plants or works.</li> <li>• Shut down the plants when not in used.</li> </ul>
Waste and Chemical Management	<ul style="list-style-type: none"> <li>• Provided on-site sorting prior to disposal.</li> <li>• Followed requirements and procedures of the “Trip-ticket System”</li> <li>• Predicted required quantity of concrete accurately.</li> <li>• Collected the unused fresh concrete at designated locations in the sites for subsequent disposal.</li> </ul>
Ecology	<ul style="list-style-type: none"> <li>• Implementing water control measures (ETWB TCW No. 5/2005) to avoid direct or indirect impacts any watercourses and impact to any aquatic fauna during the construction phase.</li> <li>• Demarcation fencing has been erected to prevent unauthorised encroachment into the riparian corridor by constructions works and traffic.</li> <li>• The construction work and site formation have been phased in order to reduce overall noise disturbance impacts in particular areas.</li> <li>• Works have been restricted to daytime and any construction lighting was designed and positioned as to not impact on adjacent ecologically sensitive areas.</li> </ul>
General	<ul style="list-style-type: none"> <li>• The site was generally kept tidy and clean.</li> <li>• Environmental Permit was displayed at site entrance.</li> </ul>

**12.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH**

12.2.1 According to the information provided by HCTYJV, the forthcoming construction activities for Contract 1 are listed below:

- Tactile tile installation works
- Planting works
- Traffic Sign Installation works
- Installation Type 2 Railing

12.2.2 According to the information provided by Sang Hing, the forthcoming construction activities for Contract 2 are listed below:

- Construction of footpath at Lin Ma Hang Road
- Watermain pipe and sewer installation work at Man Kam To Road
- Planting works at Sandy Ridge and Lin Ma Hang Road

**12.3 KEY ISSUES FOR THE COMING MONTH**

12.3.1 The construction activities are illustrated in [Appendix P](#). Key issues to be considered in the coming month for the works of Contract 1 and 2 shown in [Table 12-2](#) and [Table 12-3](#).

**Table 12-2 Work Undertaken and Illustrations of Mitigation Measures for Contract 1**

Description of Construction Activities	Used on PME	Environmental Mitigation Measures
Paving block installation works	<ul style="list-style-type: none"> <li>• Crane lorry</li> <li>• Compaction roller</li> </ul>	<ul style="list-style-type: none"> <li>• Provided efficient silt removal facilities to reduce SS level before effluent discharge.</li> <li>• Exposed slopes surface were compacted and covered with tarpaulin or similar means.</li> <li>• Maintain damp / wet surface on access road.</li> <li>• Maintain low vehicular speed within the works areas.</li> <li>• Provided vehicle wheel washing facilities at each construction site exit;</li> <li>• Stockpiles of dusty material were covered with impervious sheeting.</li> <li>• Provided workers to clear dusty materials at the vehicle entrance or exit regularly.</li> <li>• Restricted operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday.</li> <li>• Keep good maintenance of plants.</li> <li>• Provided noise barriers or hoarding to enclose the noisy plants or works.</li> <li>• Shut down the plants when not in used.</li> <li>• Provided on-site sorting prior to disposal.</li> <li>• Followed requirements and procedures of the “Trip-ticket System”</li> <li>• Works have been restricted to daytime and any construction lighting was designed and positioned as to not impact on adjacent ecologically sensitive areas.</li> <li>• The site was generally kept tidy and clean.</li> </ul>
Planting works	<ul style="list-style-type: none"> <li>• Crane Lorry</li> </ul>	
Installation of Type 2 Railing	<ul style="list-style-type: none"> <li>• Crane lorry</li> </ul>	

**Table 12-3 Work Undertaken and Illustrations of Mitigation Measures for Contract 2**

Construction Activities	Used on PME	Environmental Mitigation Measures
Construction of footpath at Lin Ma Hang Road	<ul style="list-style-type: none"> <li>• Dump truck</li> <li>• Excavator</li> </ul>	<ul style="list-style-type: none"> <li>• Provided efficient silt removal facilities to reduce SS level before effluent discharge.</li> <li>• Exposed slopes surface were compacted and covered with</li> </ul>

Construction Activities	Used on PME	Environmental Mitigation Measures
Watermain pipe and sewer installation works at Man Kam To Road	<ul style="list-style-type: none"> <li>● Excavator</li> </ul>	tarpaulin or similar means. <ul style="list-style-type: none"> <li>● Maintain damp / wet surface on access road.</li> <li>● Maintain low vehicular speed within the works areas.</li> <li>● Provided vehicle wheel washing facilities at each construction site exit.</li> </ul>
Planting works at Sandy Ridge and Lin Ma Hang Road	<ul style="list-style-type: none"> <li>● Excavator</li> <li>● Roller</li> <li>● Dump truck</li> </ul>	<ul style="list-style-type: none"> <li>● Provided water spraying for all active works area, in particular for the soil nail works.</li> <li>● Stockpiles of dusty material were covered with impervious sheeting.</li> <li>● Provided workers to clear dusty materials at the vehicle entrance or exit regularly.</li> <li>● Restricted operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday.</li> <li>● Keep good maintenance of plants.</li> <li>● Placed noisy plants away from residence and school.</li> <li>● Provided noise barriers or hoarding to enclose the noisy plants or works.</li> <li>● Shut down the plants when not in used.</li> <li>● Provided on-site sorting prior to disposal.</li> <li>● Followed requirements and procedures of the “Trip-ticket System”</li> <li>● Predicted required quantity of concrete accurately.</li> <li>● Collected the unused fresh concrete at designated locations in the sites for subsequent disposal.</li> <li>● Demarcation fencing has been erected to prevent unauthorised encroachment into the riparian corridor by constructions works and traffic.</li> <li>● Works have been restricted to daytime and any construction lighting was designed and positioned as to not impact on adjacent ecologically sensitive areas.</li> <li>● The site was generally kept tidy and clean.</li> </ul>

12.3.2 The Contractors are reminded to pay special attention on water quality mitigation measures and should fully implement the measures as recommended in the EM&A Manual, in particular to prevent surface runoff and other pollutants from flowing to local stream and Conservation Area.

### 13. CONCLUSIONS AND RECOMMENTATIONS

#### 13.1 CONCLUSIONS

- 13.1.1 This is the **55<sup>th</sup>** Monthly EM&A Report presenting the monitoring results and inspection findings for the period of **1<sup>st</sup>** to **28<sup>th</sup> February 2023**.
- 13.1.2 In the Reporting Month, no 24-hour or 1-hour TSP monitoring result that triggered the Action or Limit Levels was recorded. No NOEs or the associated corrective action was therefore required.
- 13.1.3 In the Reporting Month, no noise complaint (which triggered Action Level) was received and no Limit Level exceedance for noise monitoring exceedance was recorded.
- 13.1.4 In the Reporting Month, no water quality monitoring exceedance was recorded.
- 13.1.5 Monthly ecological monitoring for sensitive habitat for area of Contract 1 and Contract 2 were undertaken on **11<sup>th</sup> February 2023**. After analysing survey results in February from 2019 to 2023, there was no significant drop in species richness and abundance for wetland and non-wetland habitat for area of Contract 1, but a decrease in species richness and abundance for wetland and non-wetland habitat for area of Contract 2. Yet, good site practice during construction, with reference to EM&A Manual, is required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. Unnecessary site clearance should be avoided as well. In addition, implementing proper waste disposal is necessary to reduce contamination to water and soil. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.
- 13.1.6 In the Reporting Period, there was no vegetation clearance for both Contract 1 and Contract 2, and precautionary check for the presence of nesting birds was not required to carry out.
- 13.1.7 Landscape and visual inspection at both Contracts were undertaken on **28<sup>th</sup> February 2023**. The Contractor was reminded to prevent the construction material pile within Tree Protection Zone and ensure no works is allowed within the TPZ.
- 13.1.8 In the Reporting Month, no environmental complaints, summons and prosecution were received. In addition, no complaints received and emergency events relating to violation of environmental legislation for illegal dumping and landfilling were received.
- 13.1.9 In the Reporting Month, joint site inspections for Contract 1 to evaluate the site environmental performance were carried out by the Resident Engineer, ET and the Contractor of the Contract 1 on **2<sup>nd</sup>, 9<sup>th</sup>, 16<sup>th</sup>, and 23<sup>rd</sup> February 2023**. Moreover, joint site inspections for Contract 2 by the RE, ET and the Contractor of Contract 2 were carried out on **2<sup>nd</sup>, 9<sup>th</sup>, 16<sup>th</sup>, and 23<sup>rd</sup> February 2023**. IEC attended the both Contract joint site inspection on **16<sup>th</sup> February 2023**. No non-compliance was noted during the site inspections.

#### 13.2 RECOMMENDATIONS


- 13.2.1 During dry season, the Contractors are reminded to pay special attention on the air quality mitigation measures such as wheel wash facilities, watering of haul roads, loose soil construction surface and covering of dusty materials with tarpaulin sheet should be implemented as far as practicable.
- 13.2.2 Water quality mitigation measures as recommended in the EM&A Manual should be fully implemented, in particular to prevent surface runoff and other pollutants from flowing to local stream and Conservation Area.
- 13.2.3 Construction noise would be a key environmental issue during construction phase of the Project. Noise mitigation measures such as using quiet plants and mobile noise barriers should be implemented in accordance with the EM&A requirement.

## **Appendix A**

### **Layout Plan of the Project**



## **Layout Plan of Contract CV/2016/10**

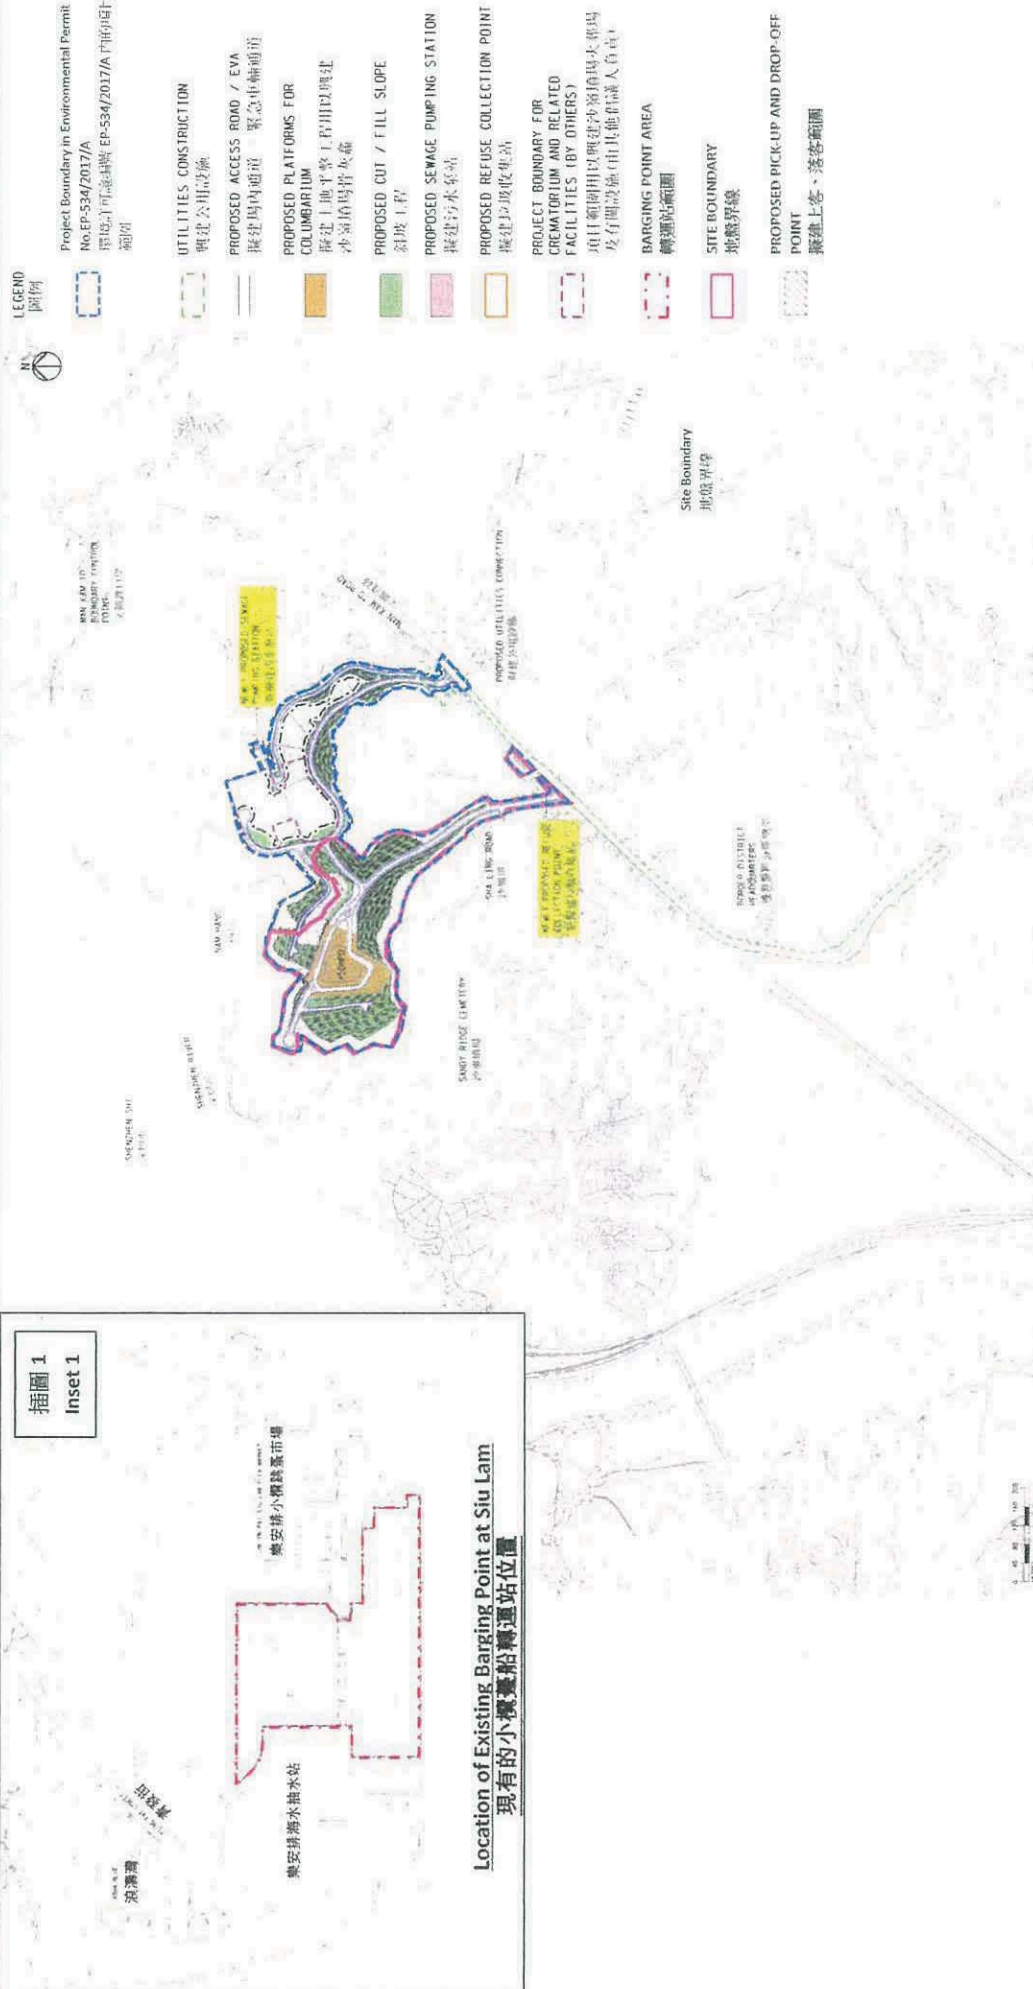


Project Title: Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery  
 工程名稱: 沙嶺墳場興建骨灰龕的工地平整及相關基建工程

Figure 1: Project Location Plan  
 圖 1: 項目位置圖

(This figure was prepared based on Figure 1 attached to the VEP Application No. VEP-555/2018 and Figures 1.3 of the Approved EIA Report No. AEIAR-198/2016)  
 (本圖是根據更改環境許可證申請文件編號: VEP-555/2018 所隨附的圖 1 和環境影響評估報告編號 AEIAR-198/2016 圖 1.3 編制)

Environmental Permit No.: FEP-01/534/2017/A  
 環境許可證編號: FEP-01/534/2017/A



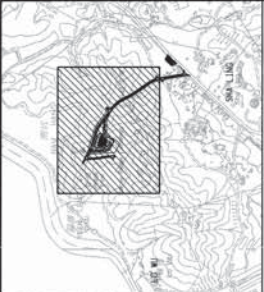

### KEY PLAN

#### LEGEND:

- PROPOSED WORKS SITE
- - - SITE FORMATION LEVEL
- +50mPD

Rev.	Description	By	Date

## ARUP

Contract No. and Title  
**Contract No. CV/2016/10**  
 Site Formation and Associated  
 Infrastructural Works for  
 Development of Columbarium at  
 Sandy Ridge Cemetery


Drawing Title  
**GENERAL LAYOUT  
 (SHEET 1 OF 3)**



Drawing No.	231448/C1/G/1001	Rev.	
Scale	1:1000	Date	12/16
Sheet No.	111000-041	Status	CONTRACT

COPYRIGHT RESERVED



土木工程拓展署  
 Civil Engineering and  
 Development Department

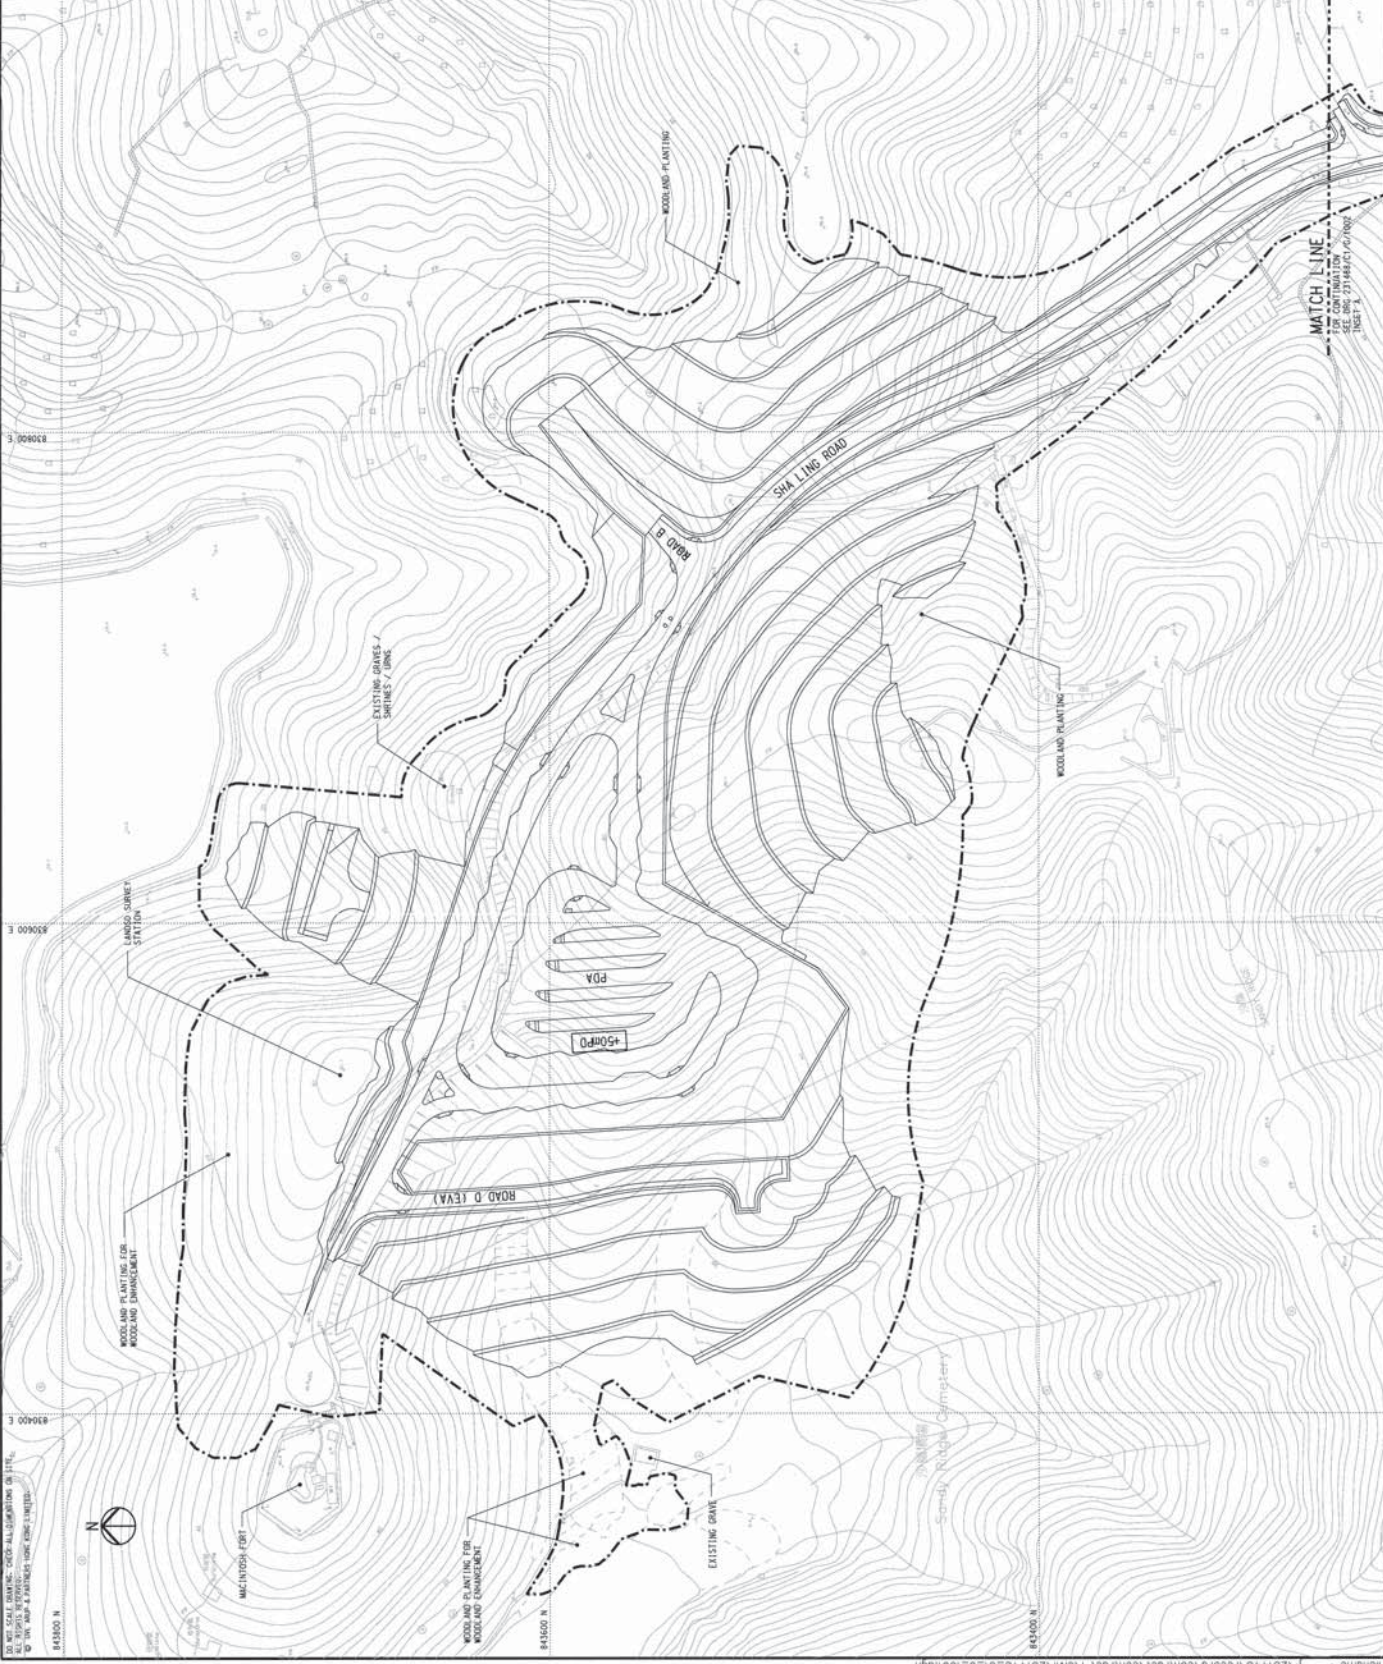

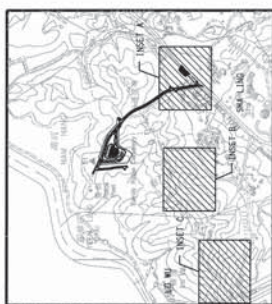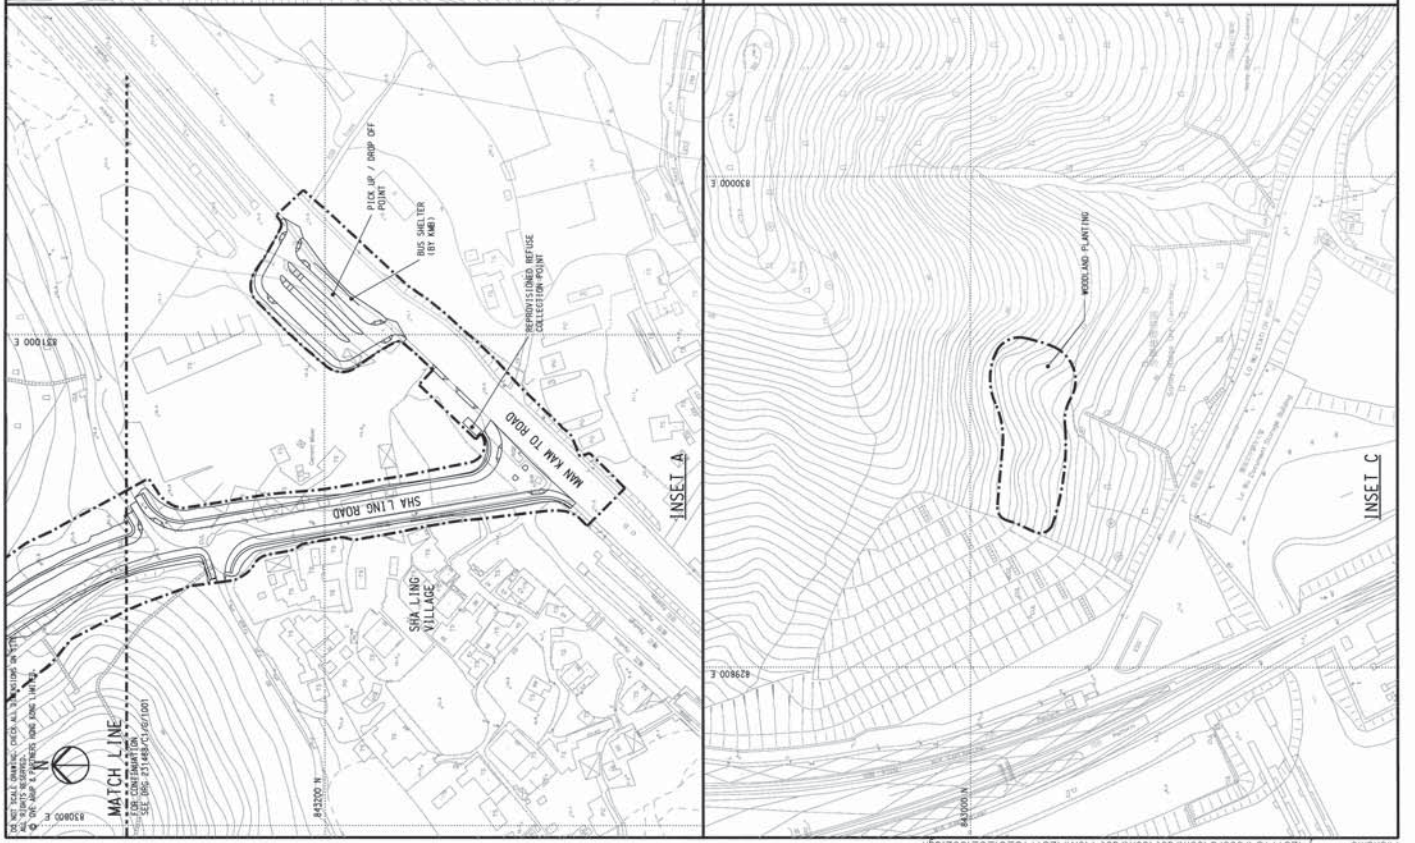

**LEGEND:**

--- ---

Rev	Description	By	Date

**ARUP**

Contract No. and Title  
**Contract No. CV2016/10**  
 Site Formation and Associated  
 Infrastructural Works for  
 Development of Columbarium at  
 Sandy Ridge Cemetery

Drawing Title  
**GENERAL LAYOUT**  
**( SHEET 2 OF 3 )**

Drawing No.	231448/C1/G/1002	Rev.	-
Scale	1:11000 MAT	Contract	CONTRACT
Date	12/16	Checked	[Signature]
Drawn	[Signature]	Drawn	[Signature]
Scale	1:11000 MAT	Drawn	[Signature]

COPYRIGHT RESERVED



DO NOT SCALE DRAWINGS (CHECK ALL DIMENSIONS ON SITE)  
 1. ALL DIMENSIONS ARE IN METERS  
 2. DIMENSIONS ARE TO FACE UNLESS OTHERWISE SPECIFIED  
 3. DIMENSIONS ARE TO FACE UNLESS OTHERWISE SPECIFIED



**KEY PLAN**

**LEGEND:**  
 - - - - - PROPOSED WORKS SITE

Rev	Description	By	Date


**ARUP**  
 Contract No. CV2016/10  
 Site Formation and Associated  
 Infrastructural Works for  
 Development of Columbarium at  
 Sandy Ridge Cemetery

Drawing Title  
**GENERAL LAYOUT  
 (SHEET 3 OF 3)**

Drawing No.	231448/C1/G/1003	Rev.	1
Town	AM	Date	12/7/16
Scale	1:1000 (M1)	Contract	CONTRACT

**CEDD**  
 土木工程拓展署  
 Civil Engineering and  
 Development Department

## **Layout Plan of Contract CV/2017/02**

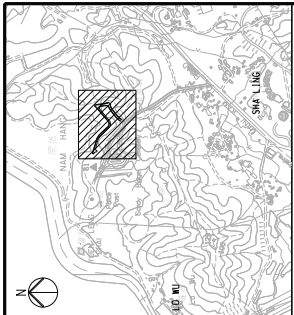

**KEY PLAN**

**LEGEND:**

--- SITE BOUNDARY


Rev	Description	By	Date
1	TENDER DRAWING	AM	11/17

**ARUP**


Contract No. and Title  
 Contract No. CV/2017/02  
 Development of Columbarium  
 at Sandy Ridge Cemetery -  
 Infrastructural Works at  
 Man Kam To Road and  
 Lin Ma Hang Road

Drawing Title  
**GENERAL LAYOUT  
 (SHEET 1 OF 5)**

Drawing No.	231448/C2/C/1001	Rev.	---
Drawn	AM	Checked	---
Date	10/17	Approved	---
Scale	1:500 (A1)	Status	TENDER

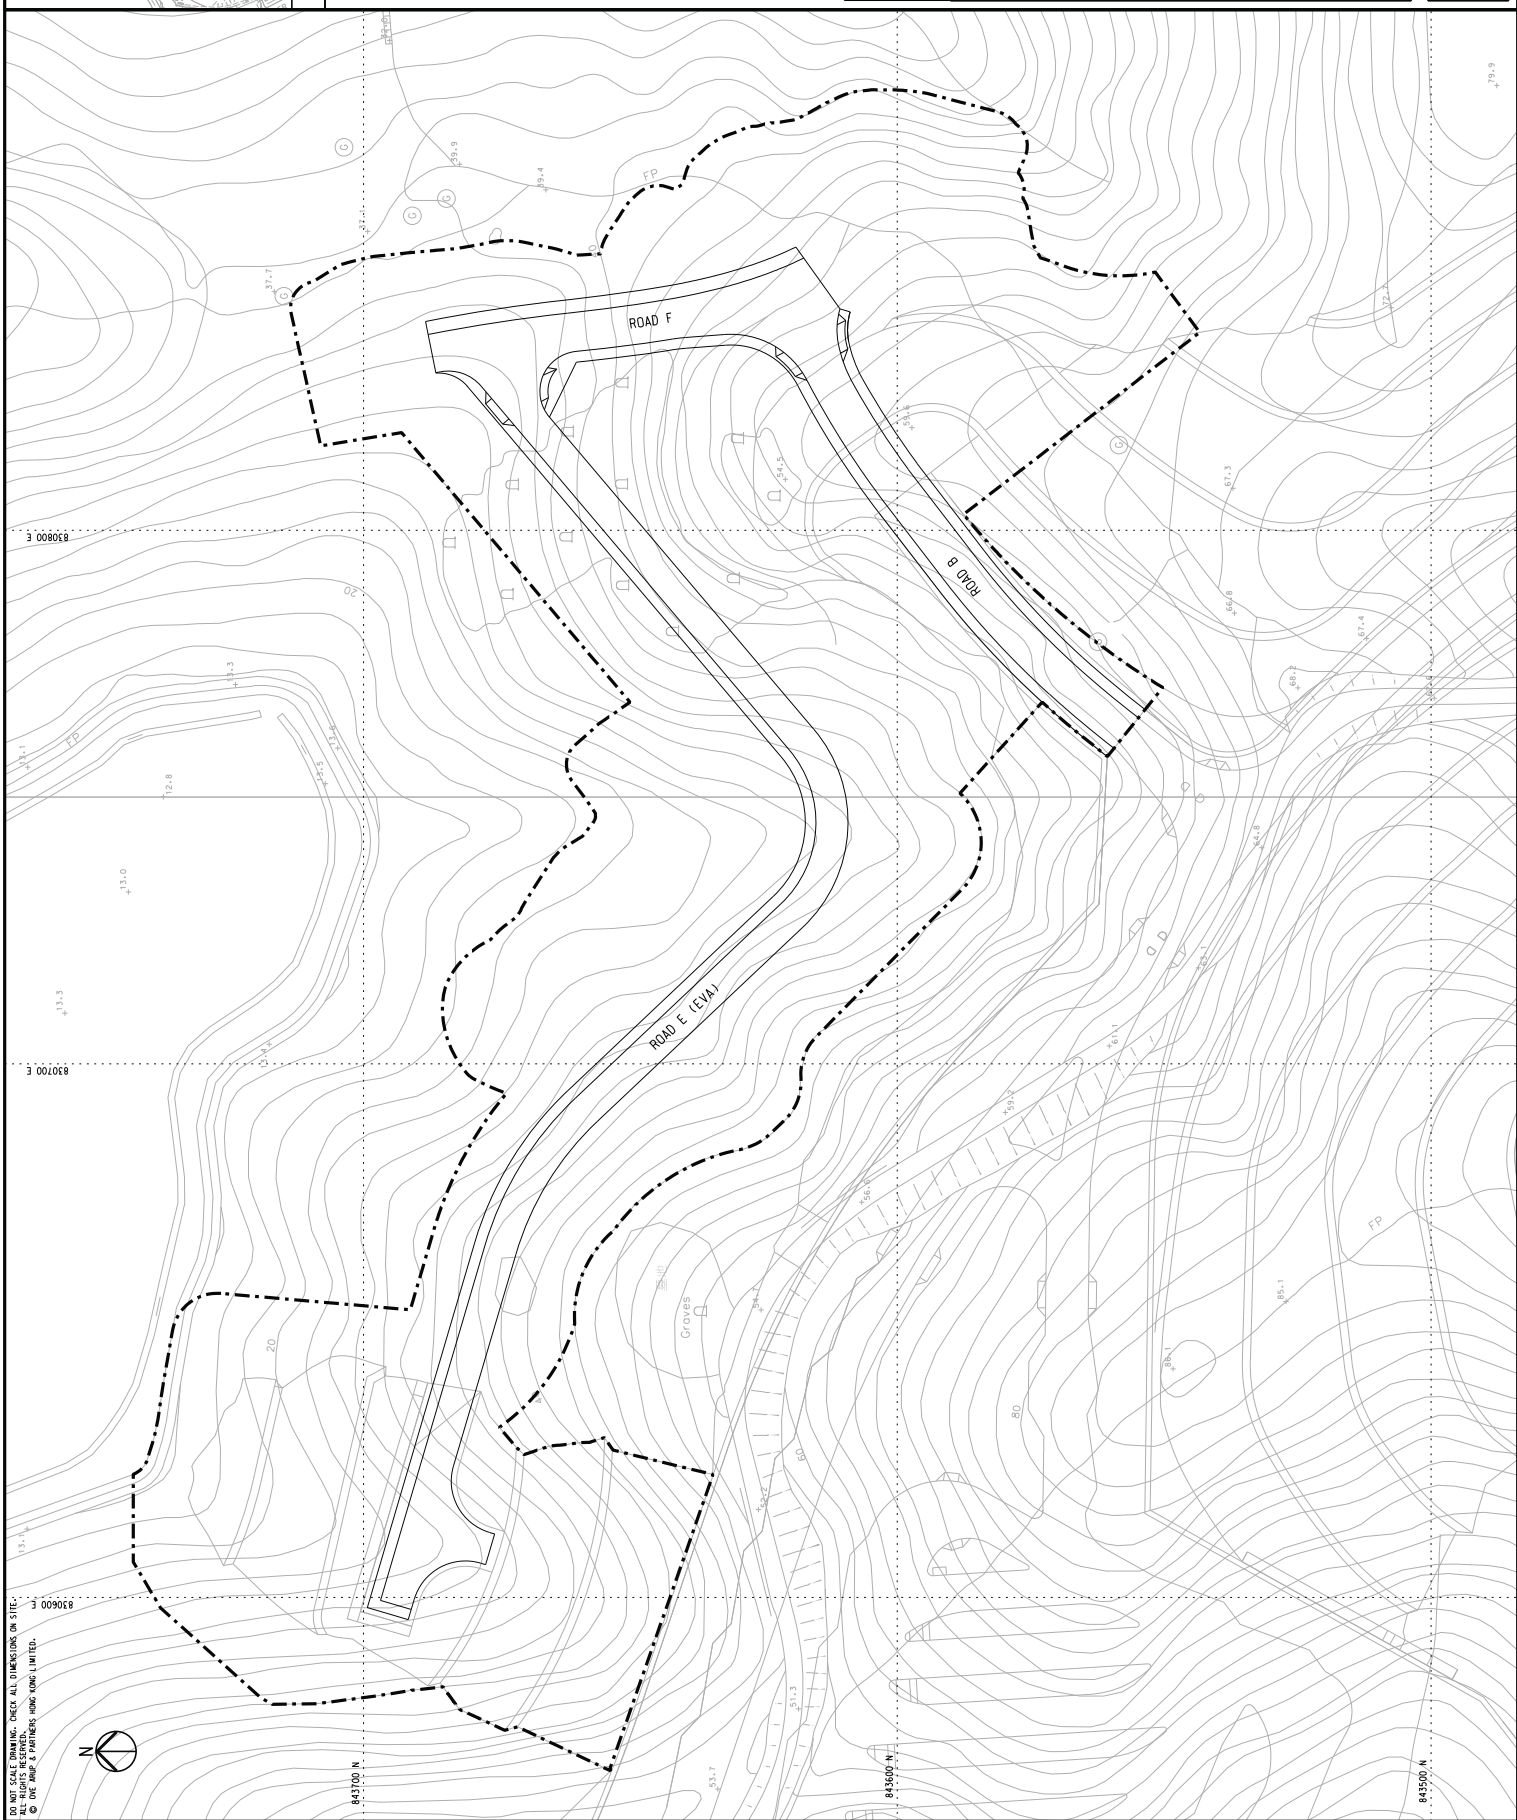

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
 ALL RIGHTS RESERVED.  
 © YUE YING & PARTNERS (HONG KONG) LIMITED.

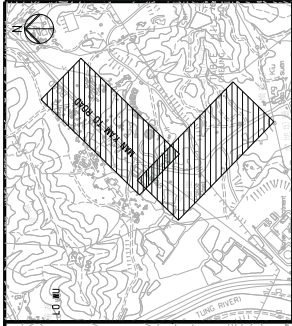

**KEY PLAN**

**LEGEND:**

--- SITE BOUNDARY

Rev	Description	By	Date
1	TENDER DRAWING	AM	11/17

**ARUP**

Contract No. and Title  
 Contract No. CV/2017/02  
 Development of Columbarium  
 at Sandy Ridge Cemetery -  
 Infrastructural Works at  
 Man Kam To Road and  
 Lin Ma Hang Road

Drawing Title  
**GENERAL LAYOUT**  
 (SHEET 2 OF 5)

Drawing No.	231448/C2/G/1002	Rev.	---
Drawn	AM	Checked	AL
Date	10/17	Approved	AL
Scale	1:1000 (A1)	Status	TENDER

Copyright Reserved  
 土木工程拓展署  
 Civil Engineering and  
 Development Department



DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
 ALL RIGHTS RESERVED.  
 © THE ARUP & PARTNERS (HK) LIMITED  
 12/27/2017





**KEY PLAN**

**LEGEND:**

--- SITE BOUNDARY

Rev	Description	By	Date
1	TENDER DRAWING	AM	11/17


**ARUP**

Contract No. CV/2017/02  
 Development of Columbarium  
 at Sandy Ridge Cemetery -  
 Infrastructural Works at  
 Man Kam To Road and  
 Lin Ma Hang Road


Drawing No.	231448/C2/G/1003	Rev.	1
Drawn	10/17	Checked	AL
Date	10/17	Approved	AL
Scale	1:1000 (A1)	Status	TENDER

Copyright Reserved

土木 工程 拓 展 署  
 Civil Engineering and  
 Development Department

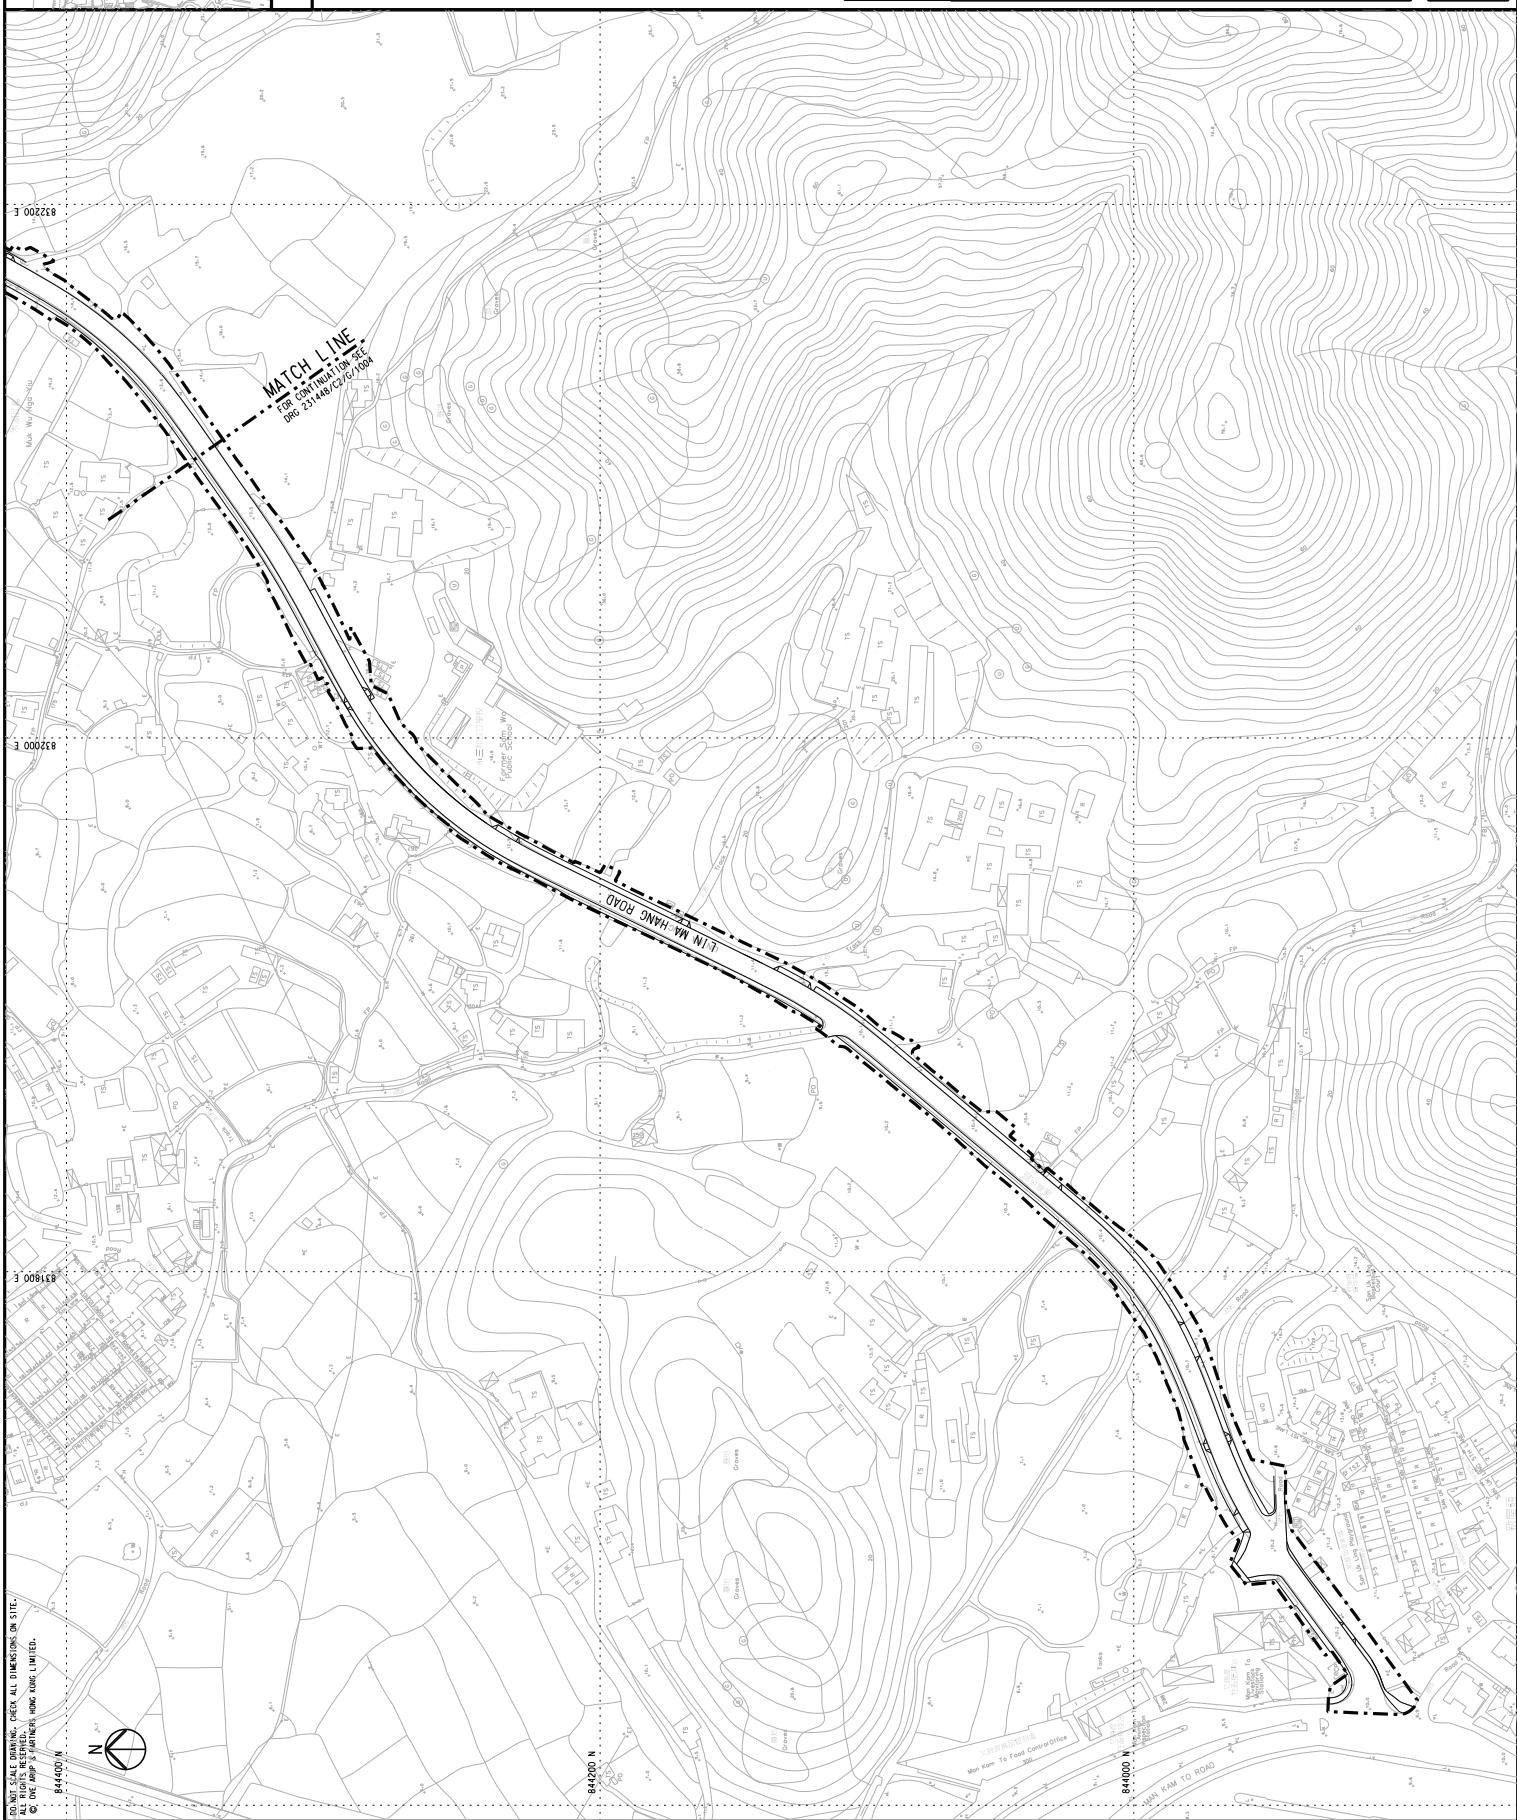

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
 ALL RIGHTS RESERVED.  
 © 2017 ARUP STANTEC CIVIL ENGINEERING LIMITED.  
 844400 N

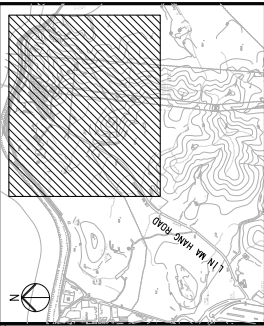

**KEY PLAN**

**LEGEND:**  
 --- SITE BOUNDARY

Rev	Description	By	Date
1	TENDER DRAWING	AM	11/17

**ARUP**

Contract No. and Title  
**Contract No. CV/2017/02**  
**Development of Columbarium**  
**at Sandy Ridge Cemetery -**  
**Infrastructural Works at**  
**Man Kam To Road and**  
**Lin Ma Hang Road**

Drawing Title  
**GENERAL LAYOUT**  
**(SHEET 4 OF 5)**

Rev.	Date	Checked	Approved
1	10/17	AL	AL


Scale: 1:1000 MAT  
 Status: TENDER  
 Drawing No.: 231448/C2/C/1004

Copyright Reserved  
 土木工程師 謝  
 Civil Engineering and  
 Development Department



DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
 ALL RIGHTS RESERVED.  
 © UIC AND P PARTNERS (HONG KONG) LIMITED.

**MATCH LINE**  
 FOR CONTINUATION SEE  
 DRG. 231448/C2/C/1004

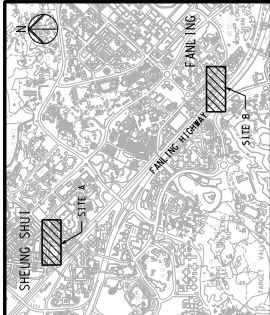

**KEY PLAN**

**LEGEND:**

--- SITE BOUNDARY

Rev	Description	By	Date
1	TENDER DRAWING	AM	11/17

**ARUP**

Contract No. and Title


Contract No. CV/2017/02  
 Development of Columbarium  
 at Sandy Ridge Cemetery -  
 Infrastructural Works at  
 Man Kam To Road and  
 Lin Ma Hang Road

Drawing title

**GENERAL LAYOUT  
 (SHEET 5 OF 5)**

Drawing No.	231448/C2/C/1005	Rev.	1
Date	10/17/17	Checked	AL
Scale	1:500 (A1)	Status	TENDER

COPYRIGHT RESERVED

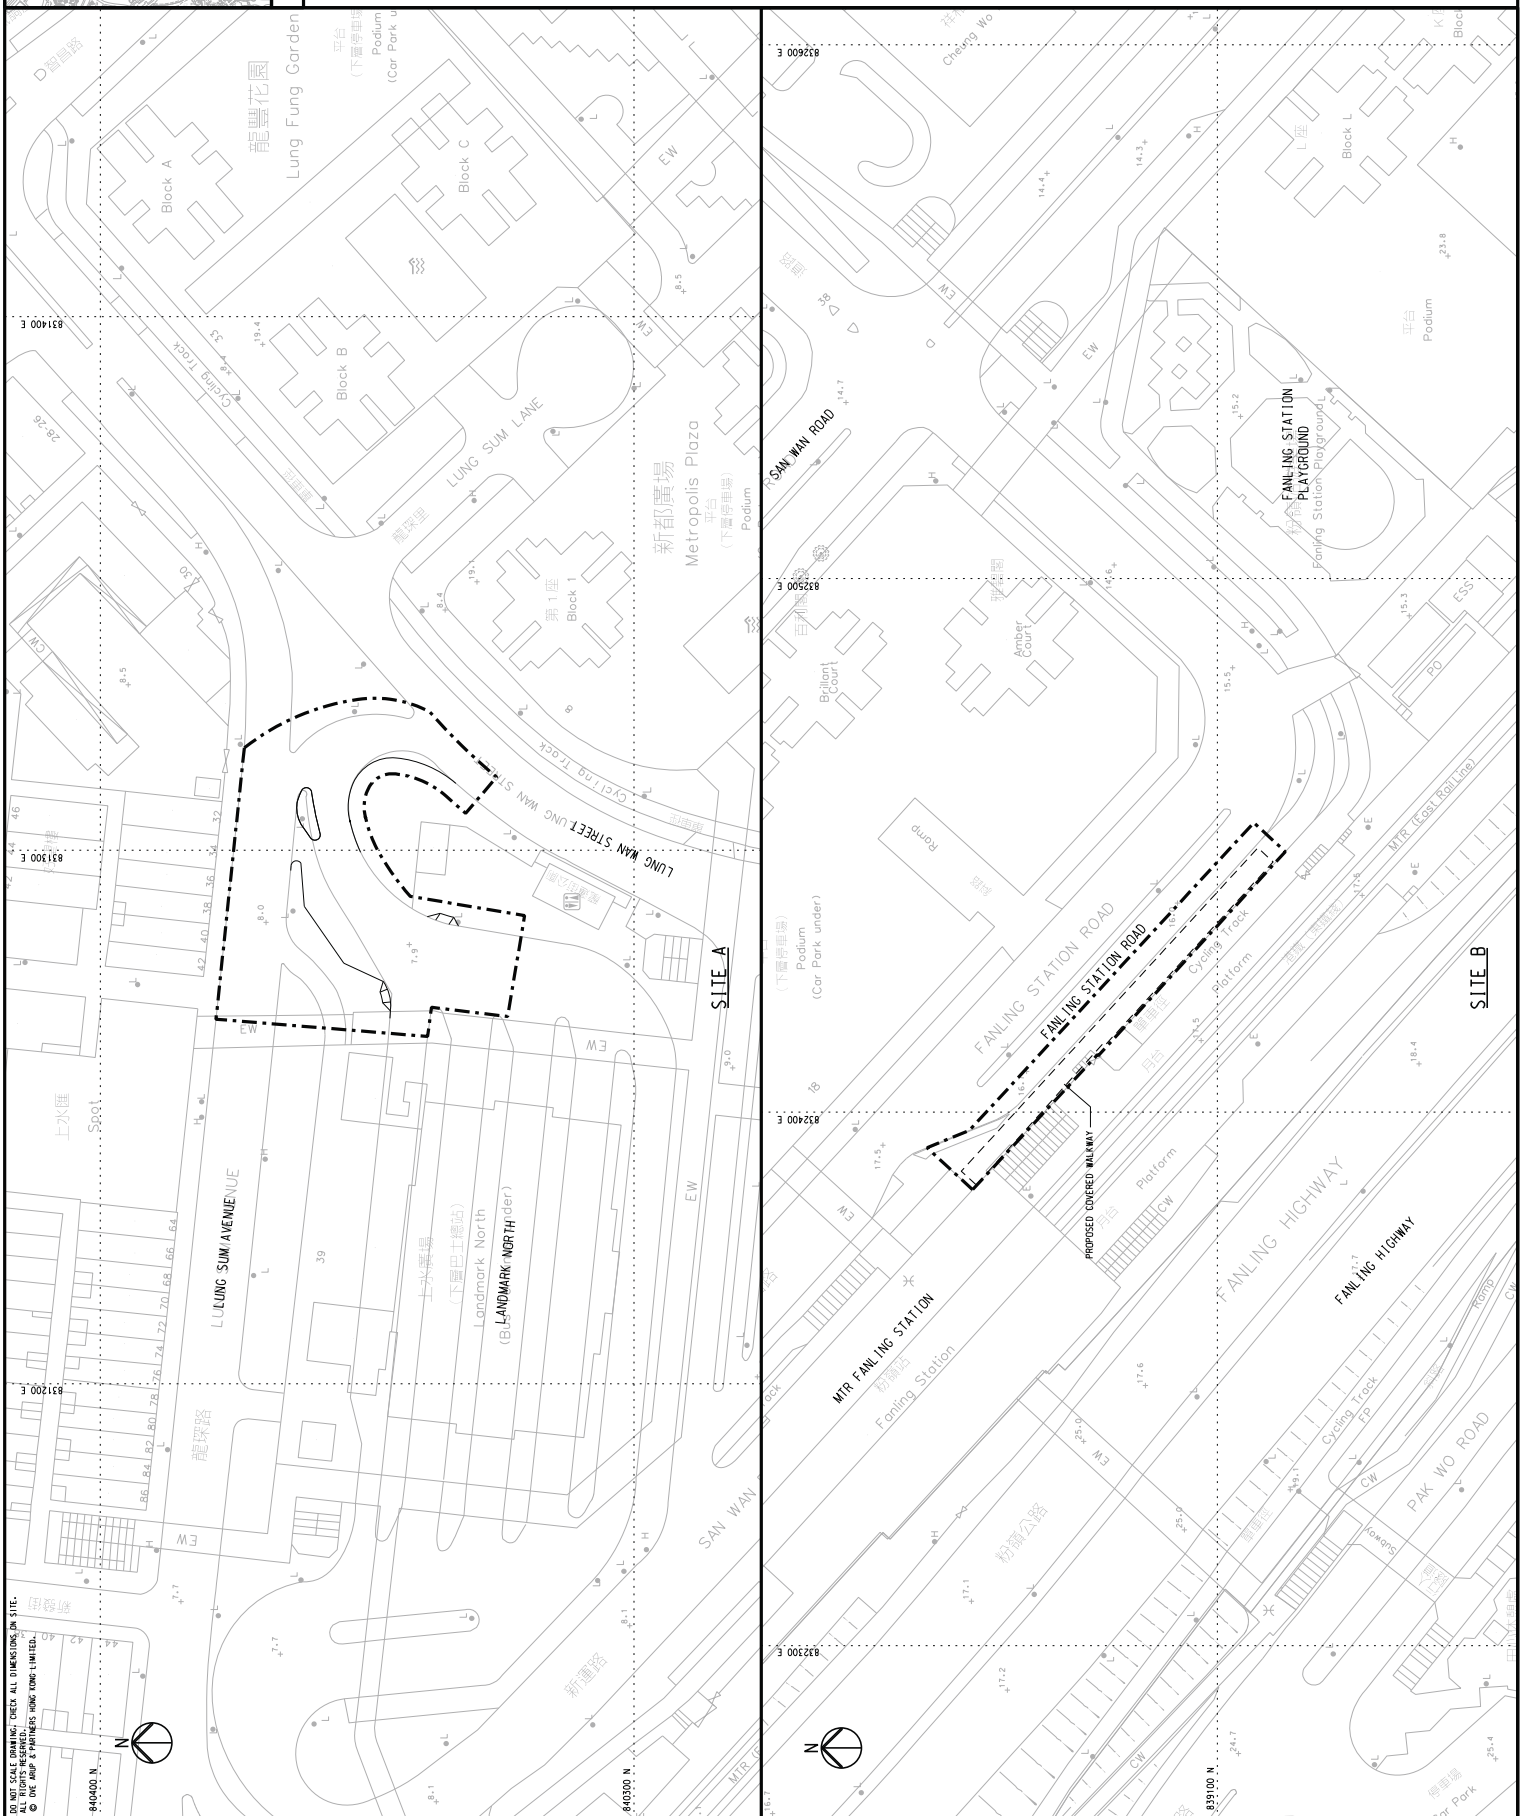


DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
 ALL RIGHTS RESERVED.  
 © UIC AND PARTNERS ENGINEERING LIMITED.

## **Appendix B**

### **Organization Structure and Contact Details of Relevant Parties**

**The Contract’s Environmental Management Organization**

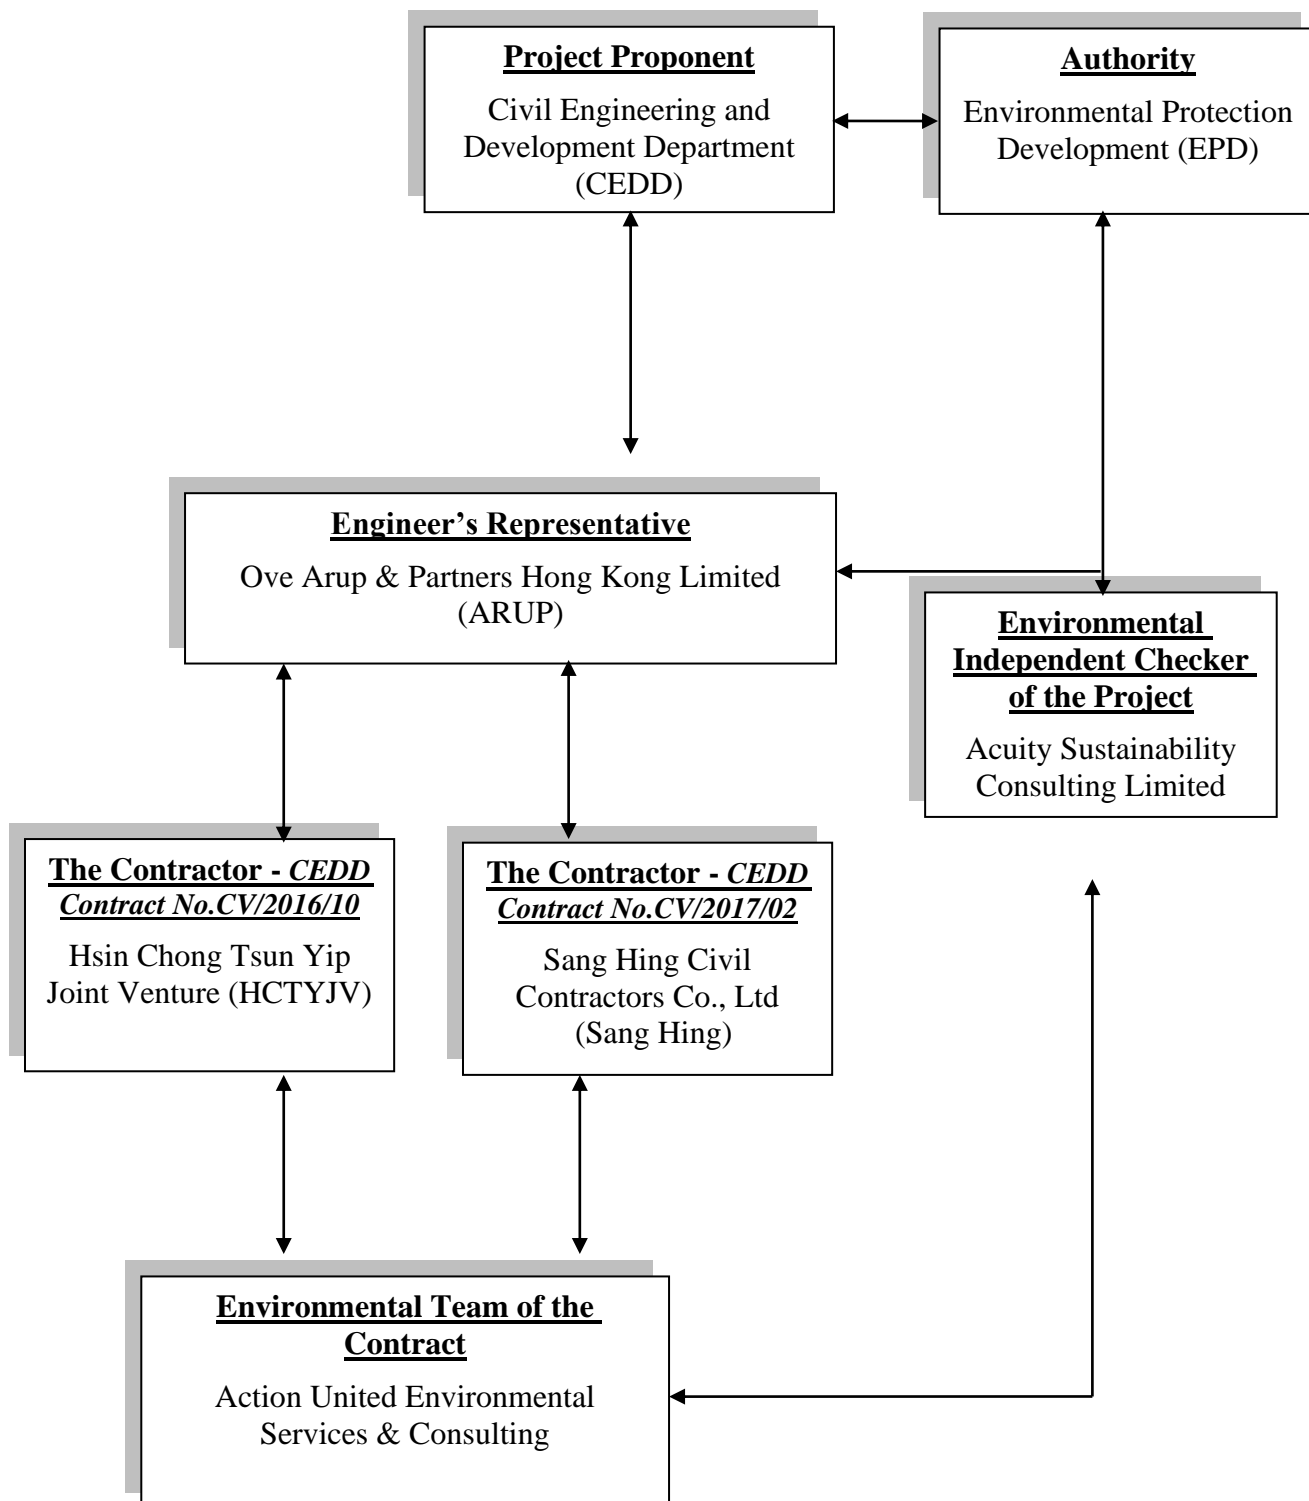

**Contact Details of Key Personnel for CV/2016/10 (Contract 1)**

<b>Organization</b>	<b>Project Role</b>	<b>Name of Key Staff</b>	<b>Tel No.</b>	<b>Fax No.</b>
CEDD	Employer	BOK Kwok-ming, Aaron	2762-5624	2714-0695
ARUP	Engineer's Representative	Steve Tang	6190-1513	2268-3950
ACUITY	Independent Environmental Checker	Mr. Leung CH Jacky	2698-6833	2698-9383
HCTYJV	Project Director	Mr. Keniel Kwong	9495-2408	2633-4691
HCTYJV	Construction Manager	Mr. Ho Man To	9620-9794	2633-4691
HCTYJV	Environmental Officer	To be advised		
HCTYJV	Environmental supervisor	Mr. Leung Pak Sum	9437-3606	2633-4691
AUES	Environmental Team Leader	Mr. T.W. Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Mr. Ben Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959-6059	2959-6079
AUES	Environmental Site Inspector	Mr. Martin Li	2959-6059	2959-6079
AUES	Qualified Ecologist	Mr. Leung Wing Keung, Mike	2959-6059	2959-6079
AUES	Qualified Ecologist	Mr. Keith L.W. Kei	2959-6059	2959-6079
AUES	Registered Landscape Architect	Mr. Shui Yau Bun, Ivan	2959-6059	2959-6079

**Legend:**

*CEDD (Employer) – Civil Engineering and Development Department*

*ARUP (Engineer) – Ove Arup & Partners Hong Kong Limited*

*HCTYJV (Main Contractor) – Hsin Chong Tsun Yip Joint Venture*

*ACUITY (IEC) – Acuity Sustainability Consulting Limited*

*AUES (ET) – Action-United Environmental Services & Consulting*

**Contact Details of Key Personnel for CV/2017/02 (Contract 2)**

<b>Organization</b>	<b>Project Role</b>	<b>Name of Key Staff</b>	<b>Tel No.</b>	<b>Fax No.</b>
CEDD	Employer	BOK Kwok-ming, Aaron	2762-5624	2714-0695
ARUP	Engineer's Representative	Anthony Lau	6190-1513	2268-3950
ACUITY	Independent Environmental Checker	Ir. Leung CH Jacky	2698-6833	2698-9383
SANG HING	Project Director	Edwin Au	9208-7329	2403-1162
SANG HING	Construction Manager	Raymond Wong	9272-1831	2403-1162
SANG HING	Site Agent	Elvin Lam	6285-0803	2403-1162
SANG HING	Environmental Officer	Keibi Chan	6090-0183	2403-1162
SANG HING	Environmental Supervisor	Kenny Chan	6115-0120	2403-1162
AUES	Environmental Team Leader	Mr. T.W. Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Mr. Ben Tam	2959-6059	2959-6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959-6059	2959-6079
AUES	Environmental Site Inspector	Mr. Martin Li	2959-6059	2959-6079
AUES	Qualified Ecologist	Mr. Leung Wing Keung, Mike	2959-6059	2959-6079
AUES	Qualified Ecologist	Mr. Keith L.W. Kei	2959-6059	2959-6079
AUES	Qualified Ecologist	Mr. N.L Lam, Alan	2959-6059	2959-6079
AUES	Registered Landscape Architect	Mr. Shui Yau Bun, Ivan	2959-6059	2959-6079

**Legend:**

*CEDD (Employer) – Civil Engineering and Development Department*

*ARUP (Engineer) – Ove Arup & Partners Hong Kong Limited*

*Sang Hing (Main Contractor) – Sang Hing Civil Contractors Co., Ltd*

*ACUITY (IEC) – Acuity Sustainability Consulting Limited*

*AUES (ET) – Action-United Environmental Services & Consulting*

## **Appendix C**

### **Three Months Rolling Programme**



**Three Months Rolling Programme of  
Contract CV/2016/10**

### 3 Month Rolling Programme (Feb 2023 to April 2023)

ID	Task Name	Duration	Start	1	2	3	4	5	6	7
1	<b>Key Dates</b>	<b>1071 days</b>	<b>Fri 15/12/17</b>							
2	Contract Starting Date	0 days	Fri 15/12/17							
3	Contract Completion Date for Section 1	1 day	Sat 29/8/20							
4	Contract Completion Date for Section 2	1 day	Fri 30/7/21							
5	Contract Completion Date for Section 3	1 day	Thu 21/11/19							
6	<b>Scheduled Completion Date</b>	<b>644 days</b>	<b>Tue 10/12/19</b>							
7	Section 1	0 days	Sat 2/10/21							
8	Section 2	0 days	Mon 14/2/22							
9	Section 3	0 days	Tue 10/12/19							
10	<b>Preliminary Works</b>	<b>144 days</b>	<b>Tue 20/2/18</b>							
11	Submission and Approval Required at Environmental Permit for Commencement of Construction	128 days	Tue 20/3/18							
12	Other Submission (Initial Survey /Tree Survey/ Condition Survey)	106 days	Tue 20/2/18							
13	<b>Section 1 of the Works (Parts A1, A2 &amp; A3)</b>	<b>1041 days</b>	<b>Thu 29/3/18</b>							
14	<b>Ground Investigation and Geotechnical instrumentation for Commencement of Slopework</b>	<b>112 days</b>	<b>Thu 29/3/18</b>							
15	Verification Drillholes (8 Nos., VDH1, 2, 7-9,8-16) / Inspection Pits and Preliminary Results Submission	114 days	Thu 29/3/18							
16	Design Review	36 days	Thu 5/7/18							
17	<b>Retaining Wall RW1</b>	<b>280 days</b>	<b>Thu 16/8/18</b>							
18	General Excavation to Formation Level	37 days	Thu 16/8/18							
19	Plate Load Test and Blinding Layer for Retaining Wall Bays 1-4	3 days	Fri 28/9/18							
20	Plate Load Test and Blinding Layer for Retaining Wall Bays 5-8	3 days	Tue 2/10/18							
21	Plate Load Test and Blinding Layer for Retaining Wall Bays 9-13	15 days	Wed 10/10/18							
22	Plate Load Test and Blinding Layer for Retaining Wall Bays 14-17	7 days	Sat 6/10/18							
23	Base slab of Retaining Wall RW1 Bay 1-4	8 days	Tue 2/10/18							
24	Base slab of Retaining Wall RW1 Bay 5-8	13 days	Mon 8/10/18							
25	Base slab of Retaining Wall RW1 Bay 9-13	17 days	Mon 22/10/18							
26	Base slab of Retaining Wall RW1 Bay 14-17	17 days	Mon 22/10/18							
27	Wall Stem of Retaining Wall RW1 Bay1-4	36 days	Thu 25/10/18							
28	Wall Stem of Retaining Wall RW1 Bay 5-8	26 days	Tue 11/12/18							
29	Wall Stem of Retaining Wall RW1 Bay 10-13	30 days	Wed 14/11/18							
30	Wall Stem of Retaining Wall RW1 Bay 14-17	23 days	Mon 26/11/18							
31	Protective Coating / Subsoil Drain / Filter Layer	5 days	Thu 14/2/19							
32	Drainage and Maintenance Access in front of RW1	75 days	Tue 26/3/19							
33	Construction CP1X & CP7X	102 days	Mon 1/4/19							
34	<b>Filling Works behind Retaining Wall and Fill Slope FS1 South (Section 12 at Drawing C1/GE/1030)</b>	<b>705 days</b>	<b>Mon 1/4/19</b>							
35	Behind Retaining Wall RW1, Filling Stage 1 (up to +25mPD)	95 days	Mon 1/4/19							
36	FS1 South , Filling (Rolling by Pass) (+25 to +27.8mPD)	10 days	Sat 20/7/19							
37	<b>FS1 South Filling Stage 2 (~2.5m, +25.0 to +27.5 mPD)</b>	<b>56 days</b>	<b>Wed 1/4/20</b>							
38	Filling (Rolling by Pass)	1 day	Wed 1/4/20							
39	<b>Filling in 3m Zone</b>	<b>28 days</b>	<b>Thu 2/4/20</b>							
40	Benching Works for Rolling by Pass Surface	3 days	Thu 2/4/20							
41	Lay Rockfill Layer (4.5/1m per 5 days)	25 days	Tue 7/4/20							
42	Drainage and Maintenance Access (+25 to +27.5 mpD)	21 days	Tue 12/5/20							
43	<b>FS1 South Filling Stage 3 (~7.5m height, +27.5 to +35mPD)</b>	<b>320 days</b>	<b>Sat 1/2/20</b>							
44	Filling (Rolling by Pass)(~7.5m, 0.5m per day)	175 days	Sat 1/2/20							
45	<b>Filling in 3m Zone</b>	<b>103 days</b>	<b>Wed 2/9/20</b>							
46	Benching Works for Rolling by Pass Surface	3 days	Wed 2/9/20							
47	Lay Rockfill Layer (7.5/1m per 5 days)	100 days	Sat 5/9/20							
48	Drainage and Maintenance Access (+27.5 to +35 mpD)	28 days	Thu 7/1/21							
49	<b>FS1 South Filling Stage 4 (~7.5m height, +35 to +42.5mPD)</b>	<b>188 days</b>	<b>Wed 2/9/20</b>							
50	Filling (Rolling by Pass)(~7.5m, 0.5m per day)	15 days	Wed 2/9/20							
51	<b>Filling in 3m Zone</b>	<b>41 days</b>	<b>Thu 7/1/21</b>							
52	Benching Works for Rolling by Pass Surface	3 days	Thu 7/1/21							
53	Lay Rockfill Layer (7.5/1m per 5 days)	38 days	Mon 11/1/21							
54	Drainage and Maintenance Access (+35 to +42.5mpD)	35 days	Sat 27/2/21							
55	<b>FS1 South Filling Stage 5 (~7.5m height, +42.5 to +50mPD)</b>	<b>536 days</b>	<b>Mon 2/12/19</b>							
56	Construction of RW11	30 days	Mon 2/12/19							
57	<b>Filling in 3m Zone</b>	<b>109 days</b>	<b>Sat 27/2/21</b>							
58	Benching Works for Rolling by Pass Surface	3 days	Sat 27/2/21							
59	Lay Rockfill Layer (7.5/1m per 5 days)	102 days	Wed 3/3/21							
60	Additional Plate Load Test at FS1	4 days	Thu 8/7/21							
61	Drainage and Maintenance Access (+42.4 to +50 mpD)	35 days	Thu 8/7/21							
62	<b>Fill Slope FS1 Middle (Section 13 at Drawing C1/GE/1030)</b>	<b>386 days</b>	<b>Mon 10/2/20</b>							
63	Drainage and Maintenance Access at toe (+13 mpD)	10 days	Mon 10/2/20							
64	<b>FS1 middle Filling Stage 1 (~7.0m max, +13.0 mPD to +20 mPD)</b>	<b>22 days</b>	<b>Fri 21/2/20</b>							
65	Filling (Rolling by Pass)(~2m, 0.5m per day)	4 days	Fri 21/2/20							
66	<b>Filling in 3m Zone</b>	<b>8 days</b>	<b>Wed 26/2/20</b>							
67	Benching Works for Rolling by Pass Surface	3 days	Wed 26/2/20							
68	Lay Filter Layer	5 days	Sat 29/2/20							
69	Drainage and Maintenance Access ( at and below+20 mpD)	10 days	Fri 6/3/20							
70	<b>FS1 middle Filling Stage 2 (~7.5m, +20.0 to +27.5 mPD)</b>	<b>53 days</b>	<b>Wed 26/2/20</b>							
71	Filling (Rolling by Pass)(~7.5m, 0.5m per day)	15 days	Wed 26/2/20							
72	<b>Filling in 3m Zone</b>	<b>23 days</b>	<b>Sat 14/3/20</b>							
73	Benching Works for Rolling by Pass Surface	3 days	Sat 14/3/20							
74	Lay Rockfill Layer (7.5m/1m per 5 day)	20 days	Wed 18/3/20							
75	Drainage and Maintenance Access (at and below+27.5 mpD)	15 days	Wed 15/4/20							
76	<b>FS1 middle Filling Stage 3 (~7.5m height, +27.5 to ~+35mPD)</b>	<b>283 days</b>	<b>Sat 14/3/20</b>							

Task Summary Progress Inactive Milestone Manual Task Manual Summary Rollup Start-only Manual Progress  
 Milestone Critical Inactive Task Inactive Summary Duration-only Manual Summary Finish-only

### 3 Month Rolling Programme (Feb 2023 to April 2023)

ID	Task Name	Duration	Start	1	2	3	4	5	6	7
77	Filling (Rolling by Pass)(~7.5m, 0.5m per day)	130 days	Sat 14/3/20							
78	<b>Filling in 3m Zone</b>	133 days	Sat 22/8/20							
79	Benching Works for Rolling by Pass Surface	3 days	Sat 22/8/20							
80	Lay Rockfill Layer (7.5m/1m per 5 day)	130 days	Wed 26/8/20							
81	Drainage and Maintenance Access (at and below +35 mpD)	20 days	Mon 1/2/21							
82	<b>FS1 middle Filling Stage 4 (~7.5m height, +35 to +42.5mPD)</b>	241 days	Sat 22/8/20							
83	Filling (Rolling by Pass)(~7.5m, 0.5m per day)	15 days	Sat 22/8/20							
84	<b>Filling in 3m Zone</b>	41 days	Sat 27/2/21							
85	Benching Works for Rolling by Pass Surface	3 days	Sat 27/2/21							
86	Lay Rockfill Layer (7.5/1m per 5 days)	38 days	Wed 3/3/21							
87	Drainage and Maintenance Access (+35 to +42.5mpD)	35 days	Tue 20/4/21							
88	<b>FS1 middle Filling Stage 5 below +42.5mPD and +50mPD)</b>	30 days	Tue 20/4/21							
89	Filling (Rolling by Pass)(~15m, 0.5m per day)	30 days	Tue 20/4/21							
90	Slope Surface forming/ Drainage and Maintenance Access	20 days	Tue 20/4/21							
91	<b>Fill Slope FS1 North (Section 14 at Drawing C1/GE/1030 )</b>	<b>900 days</b>	<b>Wed 11/7/18</b>							
92	CE16	264 days	Wed 11/7/18							
93	FS1 North Filling Works Stage 1 (+15 to+19.7mPD)	204 days	Sat 1/6/19							
94	Drainage and Maintenance Access (+15 to +20 mpD)	28 days	Sat 25/1/20							
95	Construction of Outfall CP2X	14 days	Thu 27/2/20							
96	FS1North , Filling (Rolling by Pass) (+19.7 to +22.4mPD)	20 days	Sat 14/3/20							
97	FS1 North Filling Stage 2 (+20 to +27.5 mPD)	100 days	Tue 7/4/20							
98	Drainage and Maintenance Access (+20 to +27.5 mpD)	65 days	Sat 1/8/20							
99	<b>Filling in 3m Zone (below +27.5mPD)</b>	58 days	Mon 9/3/20							
100	Benching Works for Rolling by Pass Surface	3 days	Mon 9/3/20							
101	Lay Filter Layer	5 days	Thu 12/3/20							
102	Filling by SRT (7.5m/ 3 day per 5 day)	50 days	Wed 18/3/20							
103	<b>Filling in 3m Zone (below +27.5mPD) (Rockfill)</b>	23 days	Mon 9/3/20							
104	Benching Works for Rolling by Pass Surface	3 days	Mon 9/3/20							
105	Lay Rockfill Layer (7.5m/1m per 5 day)	20 days	Thu 12/3/20							
106	Drainage and Maintenance Access	22 days	Sat 2/5/20							
107	<b>FS1 North Filling Stage 3 (+27 to +35 mPD)</b>	171 days	Tue 26/11/19							
108	Filling (Rolling by Pass)(~3m, 0.5m per day)	6 days	Tue 26/11/19							
109	Drainage and Maintenance Access (+27.5 to +35 mpD)	30 days	Fri 8/5/20							
110	<b>FS1 North Filling Stage 4 (+35 to +42.5 mPD), Upgrading of Existing Slope Feature 3NW-C/F37</b>	229 days	Fri 12/6/20							
111	Filling (Rolling by Pass)(~3m, 0.5m per day)	20 days	Fri 12/6/20							
112	Drainage and Maintenance Access (+35 to +42.5 mpD)	30 days	Sat 30/1/21							
113	<b>FS1 North Filling Stage 5 (+42.5 to +50mPD), Upgrading of Existing Slope Feature 3NW-C/F37</b>	<b>62 days</b>	<b>Wed 12/5/21</b>							
114	Filling (Rolling by Pass)(~3m, 0.5m per day)	30 days	Wed 12/5/21							
115	Drainage and Maintenance Access (+42.5 to +50 mpD)	30 days	Fri 18/6/21							
116	<b>Civil Works for Pick-up/Drop-off area (Part A1, M011 CH020 to CH140)</b>	<b>162 days</b>	<b>Sat 6/3/21</b>							
117	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>131 days</b>	<b>Sat 6/3/21</b>							
118	Sewerage Works / Drainage Works	90 days	Sat 6/3/21							
119	Watermain FW1a (CH29-100)	20 days	Wed 31/3/21							
120	Road Lighting Civil Works Provision	20 days	Thu 22/7/21							
121	Utilities (by others)	10 days	Wed 31/3/21							
122	<b>Carriageway and Footway</b>	<b>72 days</b>	<b>Sat 26/6/21</b>							
123	Backfilling to Formation Level	30 days	Sat 26/6/21							
124	Carriageway	30 days	Mon 2/8/21							
125	Footpath, Road Marking and Street Furniture	12 days	Mon 6/9/21							
126	Landscape Works	172 days	Sat 6/3/21							
127	Shrubs Planting at RW1	30 days	Wed 18/8/21							
128	Woodland Planting at Site 3	10 days	Wed 18/8/21							
129	Hydroseeding at Fill Slope	80 days	Sat 6/3/21							
130	Shrubs Planting at Pick-up/ Drop Off	10 days	Fri 23/7/21							
131	Irrigation System and Water Points (Except Water Connection)	24 days	Mon 2/8/21							
132	Tree Planting Works	10 days	Mon 20/9/21							
133	<b>Section 2 of the Works (Parts B1, B2, C, D, F, G1 &amp; G2)</b>	<b>1232 days</b>	<b>Fri 15/12/17</b>							
134	<b>Part B1</b>	<b>1103 days</b>	<b>Sat 28/4/18</b>							
135	<b>Ground Investigation and Geotechnical instrumentation for Commencement of Slopework</b>	<b>96 days</b>	<b>Sat 28/4/18</b>							
136	Verification Drillholes (10 Nos., VDH3, 6, 10-15,19-20) and Preliminary Results Submission	95 days	Sat 28/4/18							
137	Design Review	36 days	Thu 12/7/18							
138	<b>Cut Slopes CS1 &amp; CS2</b>	<b>170 days</b>	<b>Fri 12/10/18</b>							
139	Excavation (crest to +55mPD)	4 days	Fri 12/10/18							
140	Excavation (+55 to+50mPD)	11 days	Fri 12/10/18							
141	Drainage and Maintenance Access (at +55mPD berm)	55 days	Tue 16/10/18							
142	Drainage and Maintenance Access (+55 to +50 slope surface)	180 days	Tue 16/10/18							
143	<b>Cut Slope CS3</b>	<b>251 days</b>	<b>Wed 4/11/20</b>							
144	Excavation (crest to toe)	15 days	Wed 4/11/20							
145	Drainage and Maintenance Access	29 days	Sat 21/11/20							
146	Southern End of CS13	95 days	Mon 17/5/21							
147	Slope Cutting and Soil Nail	60 days	Mon 17/5/21							
148	Construction of toe wall (5 bays, approx. 66m) (4 days/ bay)	20 days	Thu 29/7/21							
149	Backfilling and drainage	15 days	Sat 21/8/21							
150	<b>Cut Slopes CS11 , CS12 and CS13</b>	<b>880 days</b>	<b>Thu 23/8/18</b>							
151	Slope Cutting (crest to+94.5mPD)	31 days	Thu 23/8/18							
152	Drainage and Maintenance Access (at crest)	29 days	Tue 2/10/18							
153	Slope Cutting and Soil Nail (+94.5 to +87mPD, 59 nos. of Soil Nail)	40 days	Sat 6/10/18							

Task Summary Progress Inactive Milestone Manual Task Manual Summary Rollup Start-only Manual Progress   
 Milestone Critical Inactive Task Inactive Summary Duration-only Manual Summary Finish-only

### 3 Month Rolling Programme (Feb 2023 to April 2023)

ID	Task Name	Duration	Start	1	2	3	4	5	6	7
154	Drainage and Maintenance Access (at +94.5mPD berm)	7 days	Fri 26/10/18							
155	Drainage and Maintenance Access (+94.5 to +87mPD slope surface)+ GI Works	24 days	Fri 26/10/18							
156	Slope Cutting and Soil Nail (+87 to+79.5mPD, 84Nos. of Soil Nail)	40 days	Thu 8/11/18							
157	Drainage and Maintenance Access (at +87mPD berm)	33 days	Fri 26/10/18							
158	RFI50 (Waiting Instruction / Abortive Works / Additional Earthwork+25m Uchannel at CS13crest)	61 days	Thu 22/11/18							
159	RFI( Slope Cutting and Soil Nail - additional 24 Nos. of Soil Nail)	39 days	Fri 11/1/19							
160	RFI50(Additional Drainage and Maintenance Access (at 87mPD berm)	13 days	Fri 1/2/19							
161	Drainage and Maintenance Access (+79.5 to +87mPD slope surface)+ GI Works	10 days	Fri 8/2/19							
162	Slope Cutting and Soil Nail (+72 to +79.5,115+21Nos. of Soil Nail)	90 days	Mon 21/1/19							
163	Drainage and Maintenance Access (at +79.5mPD berm)	42 days	Fri 1/2/19							
164	Drainage and Maintenance Access (+72 to +79.5mPD slope surface, CS13 crest)+ GI Works	13 days	Thu 2/5/19							
165	Slope Cutting and Soil Nail (+64.5 to +72 mPD, ,192 Nos. of Soil Nail)	67 days	Mon 8/4/19							
166	Drainage and Maintenance Access (at +72mPD berm)	29 days	Sat 13/4/19							
167	Drainage and Maintenance Access (+64.5 to +72mPD slope surface)+ GI Works	17 days	Wed 3/7/19							
168	Slope Cutting and Soil Nail (+57 to +64.5mPD, 521 nos. of Soil Nail, 96 nos. of Raking Drain)	180 days	Tue 2/7/19							
169	Drainage and Maintenance Access (at +64.5mPD berm)	40 days	Tue 6/8/19							
170	Drainage and Maintenance Access (+57 to +64.5mPD slope surface)+ GI Works	17 days	Fri 7/2/20							
171	Slope Cutting and Soil Nail for CS11 (+57 to +49.5 mPD, 88 nos. of Soil Nail, 19 nos. of Raking Drain)	38 days	Thu 12/3/20							
172	Drainage and Maintenance Access for CS11 (at +57mPD berm)	20 days	Thu 26/3/20							
173	Drainage and Maintenance Access for CS11 (below57 mPD slope surface/ on RW11)+ GI Works	17 days	Sat 2/5/20							
174	Slope Cutting and Soil Nail for CS12/CS13 (+57 to +49.5 mPD, 497 nos. of Soil Nail, 80 nos. of Raking Drain)	85 days	Fri 7/2/20							
175	Drainage and Maintenance Access for CS12/13 (at +57mPD berm)	35 days	Wed 11/3/20							
176	Drainage and Maintenance Access for CS12/CS13 (+49.5 to + 57mPD slope surface)+ GI Works	20 days	Sat 23/5/20							
177	Slope Cutting and Soil Nail for CS12/CS13 (+42 to +49.5 mPD, 383 nos. of Soil Nail, 87 nos. of Raking Drain)	170 days	Tue 2/6/20							
178	Drainage and Maintenance Access for CS12/13 (at +49.5mPD berm)	42 days	Fri 3/7/20							
179	Drainage and Maintenance Access for CS12/CS13 (+42 to +49.5mPD slope surface)+ GI Works	17 days	Sat 29/8/20							
180	Slope Cutting and Soil Nail for CS13 (+42 to +34.5 mPD, 126 nos. of Soil Nail, 55 nos. of Raking Drain)	59 days	Wed 23/12/20							
181	Drainage and Maintenance Access for CS13 (at +42mPD berm)	28 days	Tue 19/1/21							
182	Drainage and Maintenance Access for CS13 (+34.5 to +42mPD slope surface)+ GI Works	25 days	Tue 9/3/21							
183	Slope Cutting and Soil Nail for CS13 (+34.5 mPD to toe, 73 nos. of Soil Nail, 27 nos. of Raking Drain)	100 days	Tue 16/3/21							
184	Drainage and Maintenance Access for CS13 (at +34.5mPD berm)	27 days	Mon 12/4/21							
185	Drainage and Maintenance Access for CS13 (below+34.5 mPD slope surface)+ GI Works	21 days	Mon 19/7/21							
186	<b>Retaining Wall RW11</b>	<b>98 days</b>	<b>Tue 12/11/19</b>							
187	General Excavation with ELS to Formation Level RW11 Bay 1-4	30 days	Tue 12/11/19							
188	Plate Load Test and Blinding Layer for RW11 Bays 1-4	5 days	Tue 17/12/19							
189	Base slab of Retaining Wall RW11 Bay 1-4	10 days	Sun 22/12/19							
190	Wall Stem of Retaining Wall RW11 Bay 1-4	20 days	Mon 13/1/20							
191	Plate Load Test and Blinding Layer for RW11 Bays 5-6	5 days	Tue 17/12/19							
192	Base slab of Retaining Wall RW11 Bay 5-6	10 days	Sun 22/12/19							
193	Wall Stem of Retaining Wall RW11 Bay 5-6	20 days	Tue 7/1/20							
194	Protective Coating / Subsoil Drain / Filter Layer	5 days	Sat 8/2/20							
195	Filling Works behind Retaining Wall RW11, (~5.8m, up to +54.8mPD)	23 days	Fri 14/2/20							
196	<b>Existing Slope Upgrading Works</b>	<b>210 days</b>	<b>Tue 1/12/20</b>							
197	Existing Feature 3NW-C/C256 Rock Joint Mapping, drainage and maintenance access	150 days	Tue 1/12/20							
198	<b>Existing Feature 3NW-C/C258 Slope Upgrading Works</b>	<b>200 days</b>	<b>Mon 28/12/20</b>							
199	Slope Cutting and Soil Nail (Crest to To, 29 Nos. of Soil Nail)	100 days	Mon 28/12/20							
200	Drainage and Maintenance Access (Crest)	100 days	Fri 23/4/21							
201	<b>Cut Slope CS15, CS16 and CS17</b>	<b>753 days</b>	<b>Thu 16/8/18</b>							
202	Slope Cutting and Soil Nail (crest to+69.5mPD,25 nos. of Soil Nail)	36 days	Thu 16/8/18							
203	Drainage and Maintenance Access (at crest)	15 days	Mon 20/8/18							
204	Slope Cutting and Soil Nail (+62 to +69.5mPD, 99 nos. of Soil Nail, 37 nos. of Raking Drain)	62 days	Mon 3/9/18							
205	Drainage and Maintenance Access (at +69.5mPD berm)	49 days	Mon 3/9/18							
206	Drainage and Maintenance Access (+62 to +69.5mPD slope surface)+ GI Works	36 days	Fri 26/10/18							
207	Slope Cutting and Soil Nail (+54.5 to +62mPD, 237 nos. of Soil Nail, 58 nos. of Raking Drain)	66 days	Wed 7/11/18							
208	Drainage and Maintenance Access (at +62mPD berm)	26 days	Wed 7/11/18							
209	Drainage and Maintenance Access (+54.5 to +62mPD slope surface)+ GI Works	38 days	Sat 29/12/18							
210	Slope Cutting and Soil Nail (+47 to +54.5mPD, 548 nos. of Soil Nail, 86 nos. of Raking Drain)	155 days	Mon 7/1/19							
211	Drainage and Maintenance Access (at +54.5mPD berm)	61 days	Sat 19/1/19							
212	Drainage and Maintenance Access (+54.5 to +47mPD slope surface)+ GI Works	90 days	Wed 3/4/19							
213	Slope Cutting and Soil Nail (+39.5 to +47mPD, 490 nos. of Soil Nail, 107 nos. of Raking Drain)	94 days	Mon 6/5/19							
214	Drainage and Maintenance Access (at +47mPD berm)	38 days	Tue 2/7/19							
215	Drainage and Maintenance Access (+39.5 to +47mPD slope surface)+ GI Works	23 days	Tue 27/8/19							
216	Slope Cutting and Soil Nail (+39.5 to toe, 83 nos. of Soil Nail, 18nos. of Raking Drain)	59 days	Mon 4/5/20							
217	Drainage and Maintenance Access (at +39.5mPD berm and Slope Surface) + GI Works	45 days	Tue 5/1/21							
218	<b>Fill Slope FS17</b>	<b>52 days</b>	<b>Fri 2/7/21</b>							
219	Drainage and Maintenance Access at toe	28 days	Fri 2/7/21							
220	FS17 Filling Stage 1 (~2.5m max)	24 days	Wed 4/8/21							
221	<b>Civil Works for Sha Ling Road (M001 CH710 to CH825, MO11 CH00 to CH20, M014)</b>	<b>224 days</b>	<b>Mon 28/12/20</b>							
222	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>27 days</b>	<b>Mon 28/12/20</b>							
223	Sewerage Works / Drainage Works	18 days	Mon 28/12/20							
224	Watermain FW1 (CH532-637), FW1a (CH000-029) and FW2 (CH530-618)	15 days	Tue 12/1/21							
225	Road Lighting Civil Works Provision	8 days	Tue 12/1/21							

Task Summary Progress Inactive Milestone Manual Task Manual Summary Rollup Start-only Manual Progress  
 Milestone Critical Inactive Task Inactive Summary Duration-only Manual Summary Finish-only

ID	Task Name	Duration	Start	1	2	3	4	5	6	7
226	Utilities (by others)	3 days	Tue 12/1/21							
227	<b>Carriageway and Footway</b>	<b>57 days</b>	<b>Fri 23/7/21</b>							
228	Backfilling to Formation Level	11 days	Fri 23/7/21							
229	Carriageway	28 days	Thu 5/8/21							
230	Footpath, Road Marking and Street Furniture	18 days	Tue 7/9/21							
231	<b>Civil Works for PDA (PT04, PT05, PT06, PT07 and PT08)</b>	<b>381.1 days</b>	<b>Fri 5/6/20</b>							
232	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>238 days</b>	<b>Fri 5/6/20</b>							
233	Drainage Works (with Petrol Interceptor)	200 days	Fri 5/6/20							
234	Road Lighting Civil Works Provision	10 days	Thu 11/3/21							
235	<b>Carriageway and Footway</b>	<b>143.1 days</b>	<b>Tue 23/3/21</b>							
236	Backfilling to Formation Level	80 days	Tue 23/3/21							
237	Carriageway	60 days	Sat 10/4/21							
238	Footpath, Road Marking and Street Furniture	22 days	Thu 19/8/21							
239	<b>Civil Works for PDA (M011 CH140-215, M08 CH70-102)</b>	<b>161 days</b>	<b>Tue 9/3/21</b>							
240	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>90 days</b>	<b>Tue 9/3/21</b>							
241	Sewerage Works / Drainage Works	60 days	Tue 9/3/21							
242	Road Lighting Civil Works Provision	10 days	Mon 29/3/21							
243	Utilities (by others)	10 days	Thu 17/6/21							
244	<b>Carriageway and Footway</b>	<b>71 days</b>	<b>Tue 29/6/21</b>							
245	Backfilling to Formation Level	30 days	Tue 29/6/21							
246	Carriageway	30 days	Wed 4/8/21							
247	Footpath, Road Marking and Street Furniture	11 days	Wed 8/9/21							
248	<b>Civil Works for Sha Ling Road (M001 CH610-710)</b>	<b>114 days</b>	<b>Tue 9/3/21</b>							
249	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>44 days</b>	<b>Tue 9/3/21</b>							
250	Sewerage Works / Drainage Works	30 days	Tue 9/3/21							
251	Watermain FW1 (CH433-532) and FW2 (CH433-530)	30 days	Thu 25/3/21							
252	Road Lighting Civil Works Provision	10 days	Thu 25/3/21							
253	Utilities (by others)	10 days	Thu 25/3/21							
254	<b>Carriageway and Footway</b>	<b>70 days</b>	<b>Tue 4/5/21</b>							
255	Backfilling to Formation Level	30 days	Tue 4/5/21							
256	Carriageway	30 days	Wed 9/6/21							
257	Footpath, Road Marking and Street Furniture	10 days	Fri 16/7/21							
258	<b>Civil Works for Sha Ling Road (M001 CH480-610, M08 CH00-70)</b>	<b>555 days</b>	<b>Tue 3/3/20</b>							
259	<b>Sewage Detention Tank Civil and Structural Works</b>	<b>549 days</b>	<b>Tue 3/3/20</b>							
260	<b>Civil and Structural Works</b>	<b>74 days</b>	<b>Tue 3/3/20</b>							
261	Excavation by open cut	25 days	Tue 3/3/20							
262	Blinding layer concreting	1 day	Wed 1/4/20							
263	Construction of base slab	7 days	Thu 2/4/20							
264	Construction of wall and top slab	20 days	Wed 15/4/20							
265	Construction of manhole	7 days	Mon 11/5/20							
266	Backfilling	14 days	Tue 19/5/20							
267	VDS and AMS for Sewage Detention Tank (Permanent Design and Submission Approval)	350 days	Mon 18/5/20							
268	VDS and AMS for Sewage Detention Tank	140 days	Wed 21/7/21							
269	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>146 days</b>	<b>Tue 4/5/21</b>							
270	Sewerage Works / Drainage Works	40 days	Wed 8/9/21							
271	Watermain FW1 and FW2 (CH310-433)	17 days	Tue 4/5/21							
272	Road Lighting Civil Works Provision	18 days	Tue 25/5/21							
273	Utilities (by others)	17 days	Wed 16/6/21							
274	<b>Carriageway and Footway</b>	<b>64 days</b>	<b>Thu 28/10/21</b>							
275	Backfilling to Formation Level	12 days	Thu 28/10/21							
276	Carriageway	32 days	Thu 11/11/21							
277	Footpath, Road Marking and Street Furniture	20 days	Sat 18/12/21							
278	<b>Civil Works for Sha Ling Road (M001 CH360-480)</b>	<b>104 days</b>	<b>Wed 28/7/21</b>							
279	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>67 days</b>	<b>Wed 28/7/21</b>							
280	Sewerage Works / Drainage Works	28 days	Wed 28/7/21							
281	Watermain FW1 and FW2 (CH175-310)	18 days	Thu 19/8/21							
282	<b>Additional rising main (CE No. 181)</b>	<b>30 days</b>	<b>Thu 9/9/21</b>							
283	Road Lighting Civil Works Provision	15 days	Thu 19/8/21							
284	Utilities (by others)	11 days	Thu 19/8/21							
285	<b>Carriageway and Footway</b>	<b>37 days</b>	<b>Mon 18/10/21</b>							
286	Backfilling to Formation Level	7 days	Mon 18/10/21							
287	Carriageway	18 days	Tue 26/10/21							
288	Footpath, Road Marking and Street Furniture	12 days	Tue 16/11/21							
289	<b>Civil Works for Sha Ling Road (M001 CH180-360)</b>	<b>109 days</b>	<b>Fri 6/8/21</b>							
290	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>59 days</b>	<b>Fri 6/8/21</b>							
291	Drainage and Sewerage Works	40 days	Fri 6/8/21							
292	Watermain FW1 and FW2 (CH000-175)	23 days	Tue 7/9/21							
293	Road Lighting Civil Works Provision	22 days	Tue 7/9/21							
294	Utilities (by others)	32 days	Tue 7/9/21							
295	<b>Carriageway and Footway</b>	<b>50 days</b>	<b>Mon 18/10/21</b>							
296	Backfilling to Formation Level	10 days	Mon 18/10/21							
297	Carriageway	24 days	Fri 29/10/21							
298	Footpath, Road Marking and Street Furniture	16 days	Fri 26/11/21							
299	<b>Part B2, G1 and G2</b>	<b>1232 days</b>	<b>Fri 15/12/17</b>							
300	Access Date for Part G1 and G2	0 days	Tue 5/2/19							

Task Summary Progress Inactive Milestone Manual Task Manual Summary Rollup Start-only Manual Progress  
 Milestone Critical Inactive Task Inactive Summary Duration-only Manual Summary Finish-only

ID	Task Name	Duration	Start	1	2	3	4	5	6	7
301	<b>Land Decontamination Works</b>	<b>293 days</b>	<b>Tue 2/10/18</b>							
302	Re-appraisal and Contamination Assessment Plan (CAP) Submission to EPD	10 days	Tue 2/10/18							
303	EPD Review and Acceptance for CAP	195 days	Fri 12/10/18							
304	Environmental SI for Determination of Decontamination and SI Testing	70 days	Tue 28/5/19							
305	Contamination Assessment Report (CAR) Submission to EPD	18 days	Tue 20/8/19							
306	EPD Review and Acceptance for CAR	14 days	Tue 10/9/19							
307	<b>Civil Works for Sha Ling Road (M001 CH40-110)</b>	<b>717 days</b>	<b>Tue 21/5/19</b>							
308	<i>Objection from Local Village (EW16 &amp; 18)</i>	<i>355 days</i>	<i>Tue 21/5/19</i>							
309	Application for Road Closure / Road Diversion	17 days	Thu 30/7/20							
310	<b>Noise Barrier Bay 5 to Bay 8</b>	<b>322 days</b>	<b>Wed 19/8/20</b>							
311	General Excavation with ELS to Formation Level Bay 5 to Bay 8	15 days	Wed 19/8/20							
312	Base slab of Noise Barrier Bay 5 to Bay 8	30 days	Thu 20/8/20							
313	Wall Stem of Noise Barrier Bay 5 to Bay 8	30 days	Thu 24/9/20							
314	Protective Coating /Temp Fill	5 days	Mon 2/11/20							
315	Installation of panel	10 days	Mon 6/9/21							
316	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>70 days</b>	<b>Thu 13/5/21</b>							
317	Sewerage Works / Drainage Works	35 days	Thu 13/5/21							
318	Watermain FW3 (CH045-105)	20 days	Wed 14/7/21							
319	Road Lighting Civil Works Provision	10 days	Fri 25/6/21							
320	Utilities (by others)	15 days	Fri 25/6/21							
321	<b>Carriageway and Footway</b>	<b>59 days</b>	<b>Fri 6/8/21</b>							
322	Backfilling to Formation Level	10 days	Fri 6/8/21							
323	Carriageway	42 days	Wed 18/8/21							
324	Footpath, Road Marking and Street Furniture	7 days	Fri 8/10/21							
325	<b>Ground Investigation and Geotechnical instrumentation for Commencement of Slopework</b>	<b>45 days</b>	<b>Fri 8/2/19</b>							
326	Trial Pit Excavation / Installation of Instruments and Preliminary Results Submission	45 days	Fri 8/2/19							
327	<b>Fill Slope FS13 and FS14</b>	<b>56 days</b>	<b>Fri 6/8/21</b>							
328	Drainage and Maintenance Access at toe	32 days	Fri 6/8/21							
329	FS13 and FS14 Filling Stage 1 (~2.5m max)	24 days	Mon 13/9/21							
330	<b>Cut Slope CS14</b>	<b>20 days</b>	<b>Wed 13/10/21</b>							
331	Slope Cutting (crest to toe)	3 days	Wed 13/10/21							
332	Drainage and Maintenance Access (at crest)	17 days	Mon 18/10/21							
333	<b>Civil Works for Sha Ling Road (M001 CH110-180)</b>	<b>104 days</b>	<b>Fri 8/10/21</b>							
334	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>45 days</b>	<b>Fri 8/10/21</b>							
335	Sewerage Works / Drainage Works	30 days	Fri 8/10/21							
336	Watermain FW3 (CH105-175)	12 days	Sat 13/11/21							
337	Road Lighting Civil Works Provision	10 days	Sat 13/11/21							
338	Utilities (by others)	15 days	Sat 13/11/21							
339	<b>Carriageway and Footway</b>	<b>59 days</b>	<b>Wed 1/12/21</b>							
340	Backfilling to Formation Level	10 days	Wed 1/12/21							
341	Carriageway	42 days	Mon 13/12/21							
342	Footpath, Road Marking and Street Furniture	7 days	Mon 7/2/22							
343	<b>Man Kam To Road Bus Shelter (PT01, PT02 and PT03)</b>	<b>1175 days</b>	<b>Fri 15/12/17</b>							
344	Used as Temporary Site Office / Storage Area	340 days	Fri 15/12/17							
345	Investigation for DongJiang Watermain(CE23)	82 days	Thu 10/1/19							
346	<i>Works Area Handing Over to WSD as Request</i>	<i>198 days</i>	<i>Mon 15/4/19</i>							
347	<i>Interface Issue with C2 (As request by Arup to delay XP application) (Including Temp. Road Diversion)</i>	<i>290 days</i>	<i>Tue 28/5/19</i>							
348	TTA and XP Application at Man Kam To Road	14 days	Wed 20/5/20							
349	<i>Works Area Handling to WSD for DongJiang Watermain Works</i>	<i>37 days</i>	<i>Wed 25/11/20</i>							
350	<b>Waterworks / Drainage / Sewerage/ Utilities Works</b>	<b>180 days</b>	<b>Mon 11/1/21</b>							
351	Sewerage Work (Petrol Interceptor)	15 days	Fri 16/7/21							
352	Sewerage Works / Drainage Works	150 days	Mon 11/1/21							
353	Road Lighting Civil Works Provision	11 days	Fri 16/7/21							
354	Utilities (by others)	30 days	Fri 16/7/21							
355	<b>Carriageway and Footway</b>	<b>117 days</b>	<b>Fri 16/7/21</b>							
356	Backfilling to Formation Level	12 days	Fri 20/8/21							
357	Carriageway	56 days	Fri 3/9/21							
358	Footpath, Road Marking and Street Furniture	19 days	Thu 11/11/21							
359	Reinstatement to existing Man Kam To Road	5 days	Fri 16/7/21							
360	<b>Civil Works for Sha Ling Road (M001 CH00-40)</b>	<b>985 days</b>	<b>Thu 30/8/18</b>							
361	TTA and XP Application at Man Kam To Road	14 days	Fri 15/1/21							
362	<i>Works Area Handing Over to WSD as Request</i>	<i>120 days</i>	<i>Mon 6/5/19</i>							
363	<i>Work Area Handling to Sang Hing for Turn Around</i>	<i>190 days</i>	<i>Mon 6/4/20</i>							
364	<i>Works Area Handling to WSD for DongJiang Watermain Works</i>	<i>41 days</i>	<i>Wed 25/11/20</i>							
365	<b>Consent from WSD for Works Near Dong Jing Watermain</b>	<b>325 days</b>	<b>Thu 30/8/18</b>							
366	Investigation works / Trial Pits for Watermains	150 days	Thu 30/8/18							
367	Submission for Tempworks	104 days	Thu 21/2/19							
368	Approval from WSD	80 days	Tue 2/7/19							
369	<b>Noise Barrier Bay 1-4</b>	<b>196 days</b>	<b>Mon 1/2/21</b>							
370	General Excavation with ELS to Formation Level Bay 1-4	30 days	Mon 1/2/21							
371	Base slab of Noise Barrier Bay 1-4	30 days	Thu 11/3/21							
372	Wall Stem of Noise Barrier Bay 1-4	15 days	Mon 19/4/21							
373	Protective Coating /Temp Fill	5 days	Fri 7/5/21							
374	Installation of panel	10 days	Fri 17/9/21							
375	<b>Waterworks / Drainage / Sewerage/ Utilities Works (RHS + Man Kam To EB Slow Lane)</b>	<b>62 days</b>	<b>Thu 13/5/21</b>							
376	Sewerage Works / Drainage Works	54 days	Thu 13/5/21							

Task	Summary	Progress	Inactive Milestone	Manual Task	Manual Summary Rollup	Start-only	Manual Progress
Milestone	Critical	Inactive Task	Inactive Summary	Duration-only	Manual Summary	Finish-only	












### 3 Month Rolling Programme (Feb 2023 to April 2023)

ID	Task Name	Duration	Start	1	2	3	4	5	6	7
377	Watermain FW3 (CH000-045)	6 days	Mon 19/7/21							
378	Road Lighting Civil Works Provision	8 days	Mon 19/7/21							
379	Utilities (by others)	25 days	Thu 13/5/21							
380	<b>Carriageway and Footway (RHS+ Man Kan To EB Slow Lane)</b>	<b>38 days</b>	<b>Wed 28/7/21</b>							
381	Backfilling to Formation Level	10 days	Wed 28/7/21							
382	Carriageway	24 days	Mon 9/8/21							
383	Footpath, Road Marking and Street Furniture	4 days	Mon 6/9/21							
384	<b>Waterworks / Drainage / Sewerage/ Utilities Works (LHS)</b>	<b>52 days</b>	<b>Mon 6/9/21</b>							
385	Sewerage Works / Drainage Works	42 days	Mon 6/9/21							
386	Road Lighting Civil Works Provision	5 days	Thu 28/10/21							
387	Utilities (by others)	10 days	Thu 28/10/21							
388	<b>Carriageway and Footway (LHS)</b>	<b>38 days</b>	<b>Tue 9/11/21</b>							
389	Backfilling to Formation Level	10 days	Tue 9/11/21							
390	Carriageway	24 days	Sat 20/11/21							
391	Footpath, Road Marking and Street Furniture	4 days	Sat 18/12/21							
392	<b>Part C</b>	<b>902 days</b>	<b>Sat 15/12/18</b>							
393	<b>Consent from WSD for Works Near Dong Jing Watermain</b>	<b>702 days</b>	<b>Sat 15/12/18</b>							
394	Investigation works / Trial Pits for Watermains	60 days	Sat 15/12/18							
395	Submission for Tempworks	102 days	Sat 23/2/19							
396	<b>Approval from WSD (RFI No.66) &amp; Re-design the arrangement</b>	<b>546 days</b>	<b>Tue 2/7/19</b>							
397	<b>Refuse Collection Point</b>	<b>200 days</b>	<b>Tue 4/5/21</b>							
398	General Excavation with ELS to Formation	15 days	Tue 4/5/21							
399	Substructure Construction	20 days	Sat 22/5/21							
400	Superstructure Construction	45 days	Wed 16/6/21							
401	Pavement / Footpath reinstatment	90 days	Mon 9/8/21							
402	ABWF Works	120 days	Mon 9/8/21							
403	E&M and Waterworks	120 days	Mon 9/8/21							
404	<b>Landscape Works</b>	<b>274 days</b>	<b>Tue 2/3/21</b>							
405	at Cut Slope CS1, CS2, CS3	90 days	Wed 8/9/21							
406	at Cut Slope CS11, CS12, CS13	90 days	Thu 12/8/21							
407	at Cut Slope CS15, CS16, CS17	90 days	Tue 2/3/21							
408	at Fill Slope FS13, FS14, FS17	60 days	Wed 13/10/21							
409	Sha Ling Road and Man Kam To Road	30 days	Thu 23/12/21							
410	Woodland Planting at Site 1,2,4, 7, 8, 9	170 days	Tue 2/3/21							
411	Irrigation System and Water Points (Except Water Connection)	30 days	Fri 3/12/21							
412	<b>Section 3 of the Works (Part E)</b>	<b>457 days</b>	<b>Thu 31/5/18</b>							
413	<b>Ground Investigation and Geotechnical Instrumentation for Commencement of Slopework</b>	<b>64 days</b>	<b>Thu 31/5/18</b>							
414	Verification Drillholes (2 Nos., VDH4-5) and Preliminary Results Submission	43 days	Thu 31/5/18							
415	Design Review	36 days	Thu 5/7/18							
416	<b>Fill Slope FS3 (Section 17 at Drawing C1/GE/1053 )</b>	<b>424 days</b>	<b>Wed 11/7/18</b>							
417	Time Lag of CE16	100 days	Wed 11/7/18							
418	RFI046 Outfall Location	47 days	Mon 8/10/18							
419	Drainage, Maintenance Access at slope toe	63 days	Sat 16/2/19							
420	Construction of Outfall CP14X	11 days	Mon 7/1/19							
421	FS3 Filling Stage 1 (~+16 to +17.6 mPD)	121 days	Thu 6/12/18							
422	CE50-No Fine at Slope Toe	12 days	Fri 26/4/19							
423	FS Filling (+16.9 to +27.6 mPD) (Rolling by Pass)	60 days	Thu 23/5/19							
424	<b>FS Filling (+27.6 to 30 mPD) (Rolling by Pass)</b>	<b>12 days</b>	<b>Sat 3/8/19</b>							
425	FS3 Filling Stage 1 (+16.9 to +21 mPD)	41 days	Sat 17/8/19							
426	Drainage and Maintenance Access (+21 to +28.5 mpD)	19 days	Tue 8/10/19							
427	FS3 Filling Stage 2 (~-7.5m, 21 to +28.5 mPD)	10 days	Wed 30/10/19							
428	Drainage and Maintenance Access (+28.5 to +35.5mpD)	15 days	Fri 22/11/19							
429	FS3 Filling Stage 3 (~-7.5m, +28.5 to 35.5 mPD)	17 days	Thu 21/11/19							
430	<b>Retaining Wall RW4</b>	<b>96 days</b>	<b>Sat 17/8/19</b>							
431	General Excavation to Formation Level(Bay1~2)	23 days	Sat 17/8/19							
432	Plate Load Test and Blinding Layer for Retaining Wall Bays 3-8	5 days	Fri 13/9/19							
433	Plate Load Test and Blinding Layer for Retaining Wall Bays 1-2	5 days	Fri 20/9/19							
434	Base Slab of Retaining Wall RW4 Bay 1-4	16 days	Fri 20/9/19							
435	Base Slab of Retaining Wall RW4 Bay 5-8	16 days	Thu 26/9/19							
436	Wall Stem of Retaining Wall RW4 Bay 1-4	30 days	Fri 11/10/19							
437	Wall Stem of Retaining Wall RW4 Bay 5-8	20 days	Thu 17/10/19							
438	Protective Coating / Subsoil Drain / Filter Layer	5 days	Sat 9/11/19							
439	Backfilling behind RW4 and Fill Slop FS4 (~8m up to +35.5 mPD)	22 days	Fri 15/11/19							
440	<b>Fill Slope FS2</b>	<b>47 days</b>	<b>Thu 17/10/19</b>							
441	Drainage and Maintenance Access (+35.5 to +43.0 mpD)	19 days	Thu 17/10/19							
442	FS2 Filling Stage 1 (~-7.5m, +35.5 to +43 mPD)	20 days	Fri 8/11/19							
443	Drainage and Maintenance Access (+43.0 to +50 mpD)	30 days	Thu 17/10/19							
444	FS2 Filling Stage 2 (~-7.5m, +43 to +50 mPD)	18 days	Wed 20/11/19							
445	<b>Cut Slope CS18 and CS19</b>	<b>235 days</b>	<b>Mon 25/2/19</b>							
446	<b>Slope Cutting (+54.5 to crest)</b>	<b>30 days</b>	<b>Wed 27/2/19</b>							
447	Confirmation of Interface Details at CS18/19 (NCE29)	30 days	Wed 27/2/19							
448	Drainage and Maintenance Access (crest)+ GI Works	8 days	Wed 3/4/19							
449	Slope Cutting and Raking Drain (+47 to +54.5mPD, 13 nos. of Raking Drain)	113 days	Mon 25/2/19							
450	Drainage and Maintenance Access (+54.5 to +62mPD slope surface/berm)+ GI Works	30 days	Thu 4/4/19							
451	Slope Cutting and Raking Drain (+47mPD to toe, 18 nos. of Raking Drain)	110 days	Mon 6/5/19							
452	Drainage and Maintenance Access (below +47mPD slope surface/berm)+ GI Works	70 days	Sat 14/9/19							

Task Summary Progress Inactive Milestone Manual Task Manual Summary Rollup Start-only Manual Progress  
 Milestone Critical Inactive Task Inactive Summary Duration-only Manual Summary Finish-only


### 3 Month Rolling Programme (Feb 2023 to April 2023)

ID	Task Name	Duration	Start	1	2	3	4	5	6	7
453	<b>Landscape Works</b>	<b>67 days</b>	<b>Mon 16/9/19</b>							
454	at Fill Slope FS2, FS3	50 days	Tue 8/10/19							
455	at Cut Slope CS18, CS19	60 days	Mon 16/9/19							

Task		Summary		Progress		Inactive Milestone		Manual Task		Manual Summary Rollup		Start-only		Manual Progress	
Milestone		Critical		Inactive Task		Inactive Summary		Duration-only		Manual Summary		Finish-only			



**Three Months Rolling Programme of  
Contract CV/2017/02**

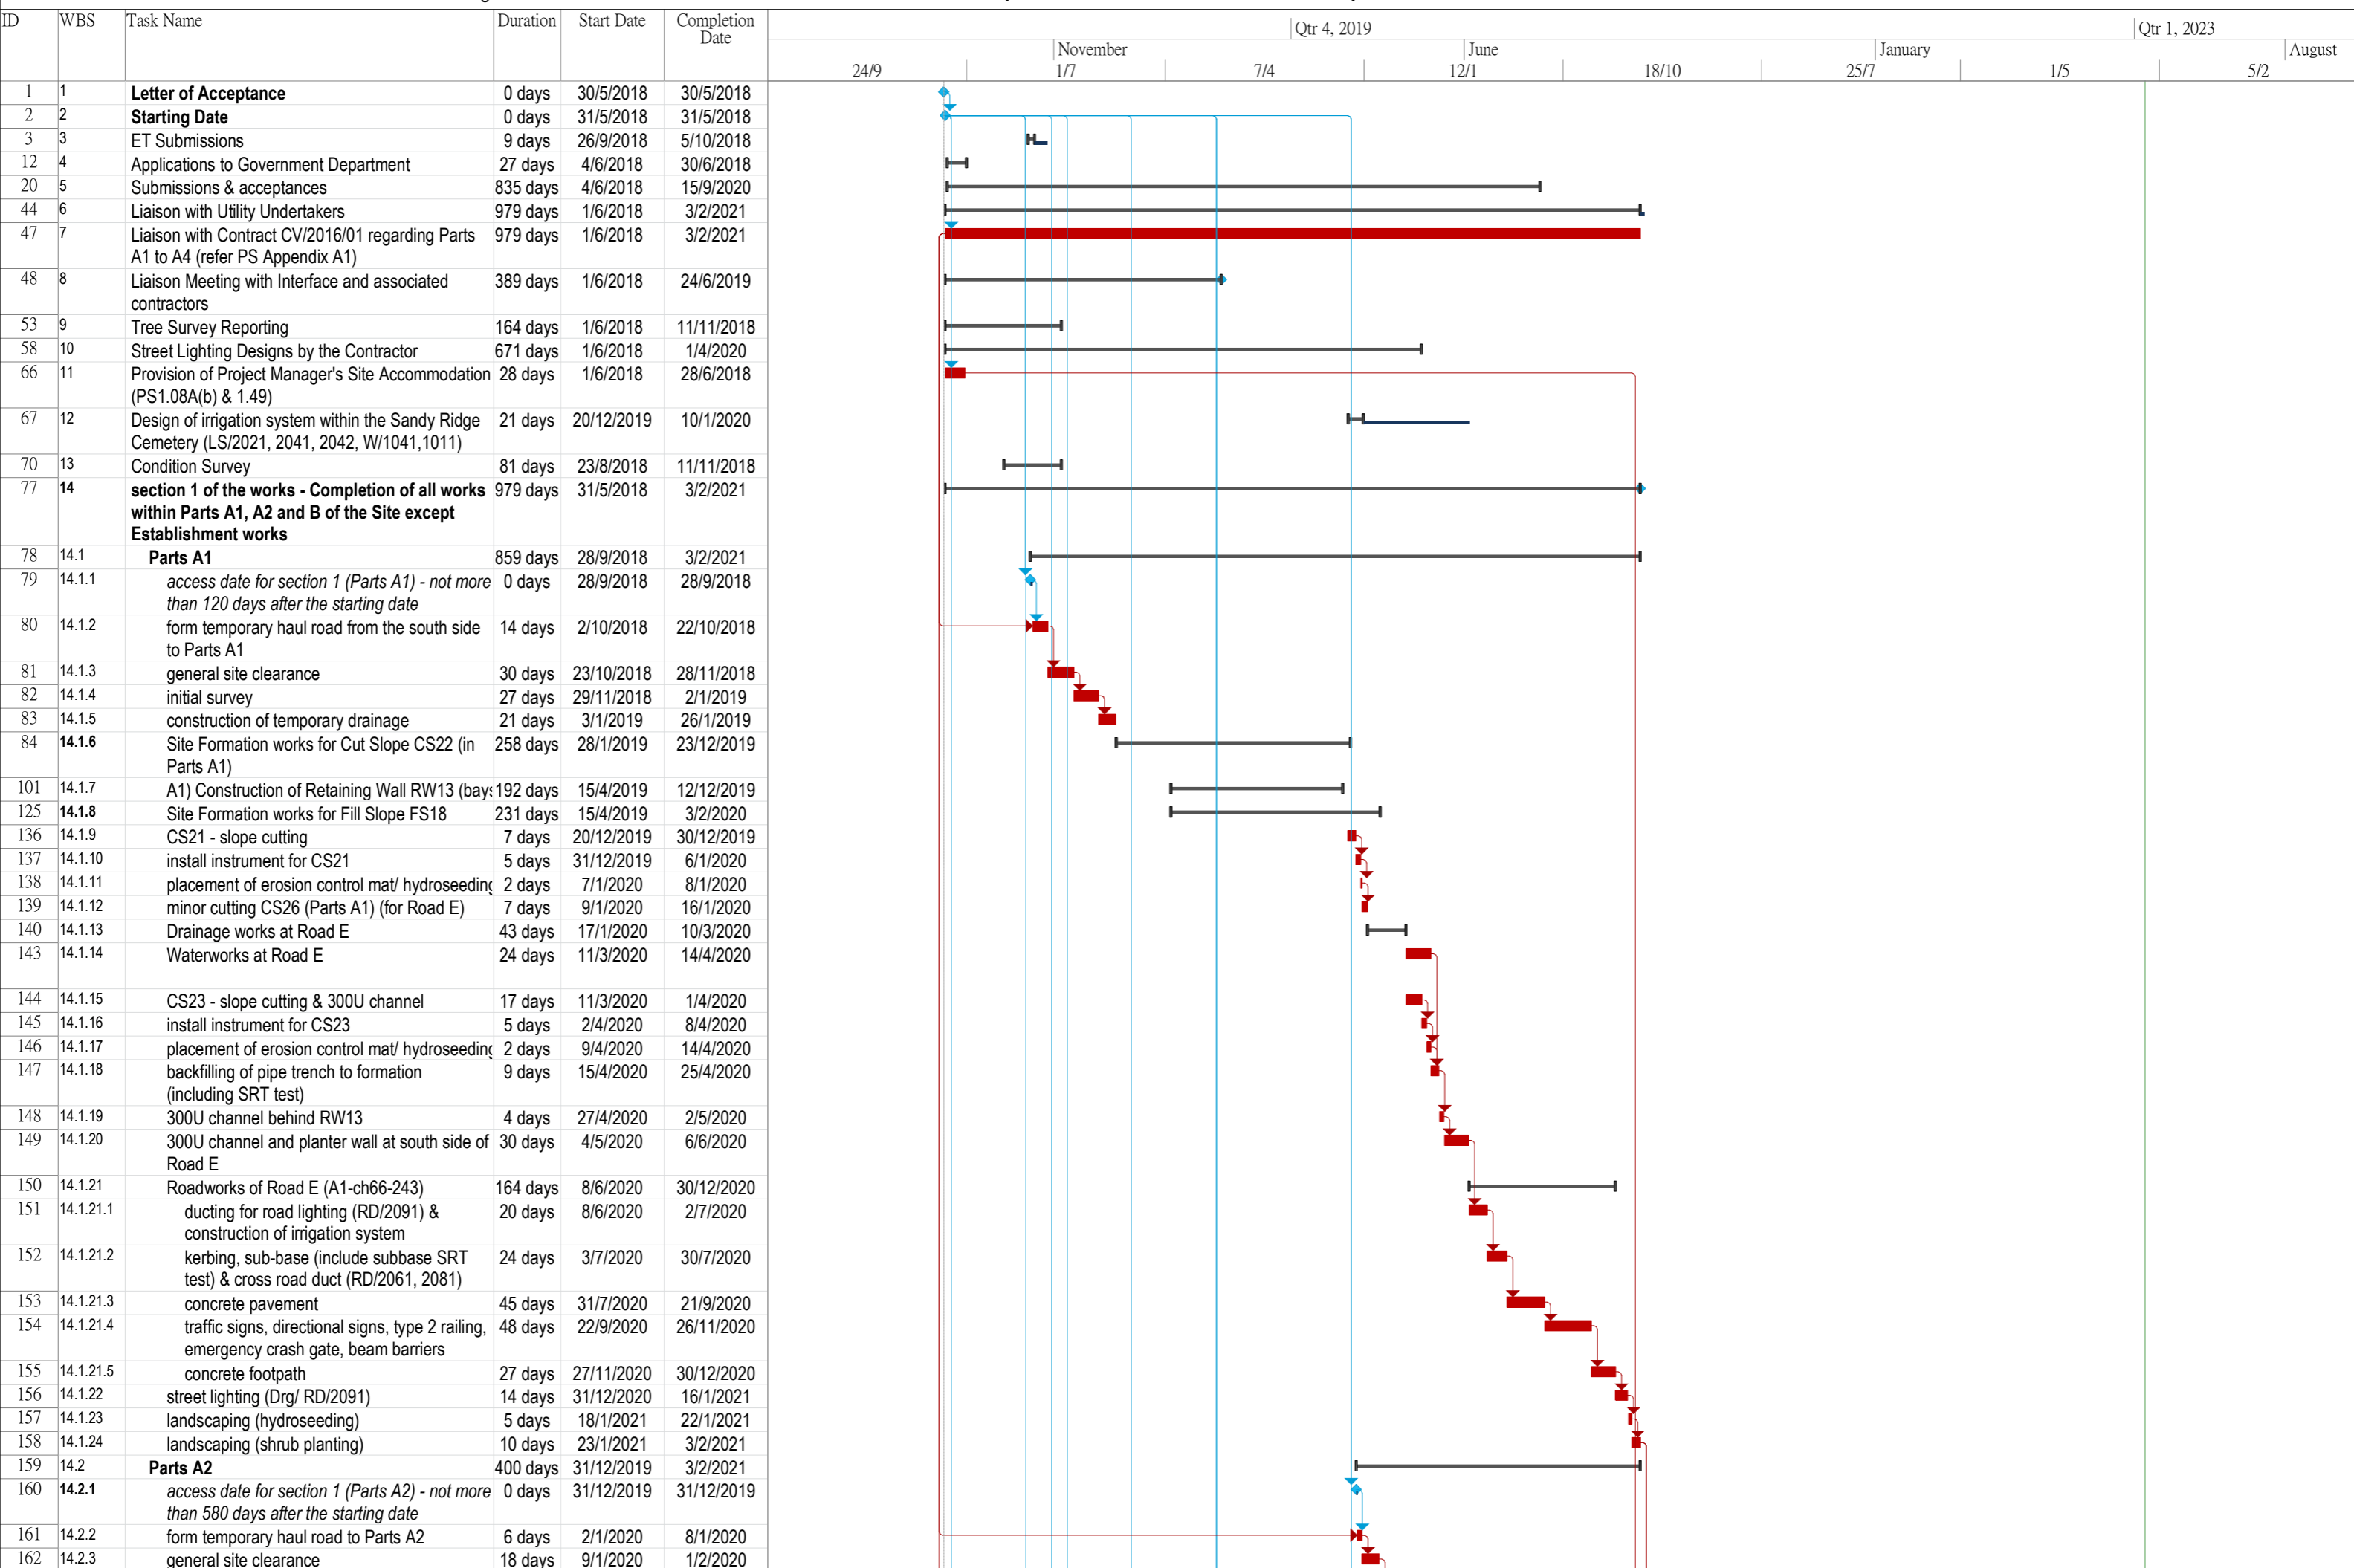



ID	WBS	Task Name	Duration	Start Date	Completion Date	Qtr 4, 2019						Qtr 1, 2023				
						November		June		January		August				
				24/9	1/7	7/4	12/1	18/10	25/7	1/5	5/2					
408	14.3.5.20	Phase 7: TTA14s	46 days	4/10/2019	27/11/2019											
417	14.3.5.21	Phase 7: additional TTA21s	29 days	24/10/2019	27/11/2019											
427	14.3.5.22	additional Phase 8: additional TTA 0s	41 days	27/11/2019	17/1/2020											
437	14.3.6	Construction of Sewerage (DN630) - refer to Drawing No. MKTR Programme/DR/001	311 days	18/1/2020	3/2/2021											
438	14.3.6.1	Phase A: TTA 1n	50 days	21/1/2020	21/3/2020											
447	14.3.6.2	Phase A: TTA 7n	52 days	18/1/2020	21/3/2020											
456	14.3.6.3	Phase B: TTA 2n	52 days	23/3/2020	28/5/2020											
465	14.3.6.4	Phase B: TTA 8n	52 days	23/3/2020	28/5/2020											
474	14.3.6.5	Phase C: TTA 3n	52 days	29/5/2020	30/7/2020											
483	14.3.6.6	Phase C: TTA 9n	52 days	29/5/2020	30/7/2020											
492	14.3.6.7	Phase D: TTA 4n	52 days	31/7/2020	29/9/2020											
501	14.3.6.8	Phase D: TTA 10n	52 days	31/7/2020	29/9/2020											
510	14.3.6.9	Phase E: TTA 5n	52 days	30/9/2020	2/12/2020											
519	14.3.6.10	Phase E: TTA 11n	52 days	30/9/2020	2/12/2020											
528	14.3.6.11	Phase F: TTA 6n	51 days	3/12/2020	3/2/2021											
537	14.3.6.12	Phase F: additional TTA 12s	38 days	18/12/2020	3/2/2021											
546	14.3.6.13	Phase F: additional TTA 0n	38 days	18/12/2020	3/2/2021											
555	15	Planned Completion for section 1 of the works	0 days	3/2/2021	3/2/2021											
556	16	Completion Date for section 1 of the works	0 days	3/2/2021	3/2/2021											
557	17	<b>section 2 of the works - Completion of all works within Parts C1 and C2 of the Site except Establishment works</b>	979 days	31/5/2018	3/2/2021											
558	17.1	access date for section 2 (Part C1)	0 days	31/5/2018	31/5/2018											
559	17.2	Temporary Traffic Arrangement (TTA) Scheme for Lin Ma Hang Road	162 days	1/6/2018	9/11/2018											
565	17.3	works at Lin Ma Hang Road (section 2 Part C1) refer Appendice LMHR01a to d	817 days	10/11/2018	3/2/2021											
566	17.3.1	Phase I (stage 1)-south lane (chainage 240-283)	23 days	10/11/2018	6/12/2018											
577	17.3.2	Phase I (stage 2)-north lane (chainage 240-283)	16 days	7/12/2018	27/12/2018											
587	17.3.3	Phase I (stage 3)-south lane (chainage 283-333)	26 days	28/12/2018	28/1/2019											
598	17.3.4	Phase I (stage 4)-north lane (chainage 283-333)	17 days	29/1/2019	20/2/2019											
608	17.3.5	Phase I (stage 5)-south lane (chainage 335-385)	18 days	21/2/2019	13/3/2019											
618	17.3.6	Phase I (stage 6)-north lane (chainage 335-385)	16 days	14/3/2019	1/4/2019											
627	17.3.7	Phase I (stage 7)-south lane (chainage 380-430)	23 days	2/4/2019	3/5/2019											
638	17.3.8	Phase I (stage 8)-north lane (chainage 380-430)	15 days	4/5/2019	22/5/2019											
648	17.3.9	Phase I (stage 9)-south lane (chainage 190-240)	18 days	23/5/2019	13/6/2019											
659	17.3.10	Phase I (stage 10)-north lane (chainage 190-240)	16 days	14/6/2019	3/7/2019											
669	17.3.11	Phase II (stage 1)-south lane (chainage 32-85)-Noise Barrier MM6 (bays 1-3) & MM7 (bays 1-2)	95 days	4/7/2019	25/10/2019											
703	17.3.12	Phase II (stage 2)-north lane (chainage 32-85)-Noise Barrier MM9 (bays 1-4)	84 days	26/10/2019	7/2/2020											
735	17.3.13	Phase II (stage 3)-south lane (chainage 85-138)	38 days	8/2/2020	23/3/2020											
746	17.3.14	Phase II (stage 4)-north lane (chainage 85-138)-Noise Barrier MM10 (bays 1-4)	68 days	24/3/2020	17/6/2020											
776	17.3.15	Phase II (stage 5)-south lane (chainage 138-190)	36 days	18/6/2020	31/7/2020											
787	17.3.16	Phase II (stage 6)-north lane (chainage 138-190)-Noise Barrier MM10 (bays 5-9)	85 days	1/8/2020	11/11/2020											
818	17.3.17	Phase II (stage 7)-south lane (chainage 0-32)-Noise Barrier MM5 (bays 1-2)	53 days	12/11/2020	15/1/2021											
851	17.3.18	Phase II (stage 8)-north lane (chainage 0-32)	16 days	16/1/2021	3/2/2021											
862	17.3.19	Noise Barrier MM8 (bays 1-3)	140 days	1/8/2020	18/1/2021											
891	17.3.20	Street lighting (drawpits, abandon existing public lighting & cable, 100uPVC ducts) (ch0-435)	21 days	14/12/2020	9/1/2021											
892	17.3.21	tree planting	3 days	11/1/2021	13/1/2021											
893	17.3.22	Street furniture & construction of footpath (ch0-435)	22 days	9/1/2021	3/2/2021											
894	17.3.23	Phase Ia (stage 101)-south lane (chainage 633-685)	20 days	10/11/2018	3/12/2018											
904	17.3.24	Phase Ia (stage 102)-north lane (chainage 633-685)	16 days	4/12/2018	21/12/2018											
914	17.3.25	Phase Ia (stage 103)-south lane (chainage 685-747)	25 days	22/12/2018	23/1/2019											
925	17.3.26	Phase Ia (stage 104)-north lane (chainage 685-747)	17 days	24/1/2019	15/2/2019											







ID	WBS	Task Name	Duration	Start Date	Completion Date	Qtr 4, 2019					Qtr 1, 2023	
						24/9	November	7/4	June	18/10	January	1/5
1519	20.1.11	design for fall arrest system of the proposed covered walkway at Fanling Station Road	150 days	15/2/2019	14/7/2019							
1520	20.1.12	submission of fall arrest system	0 days	14/7/2019	14/7/2019							
1521	20.1.13	acceptance of fall arrest system by Project Manager	0 days	4/8/2019	4/8/2019							
1522	20.1.14	Liaison with MTRC for the works arrangement	30 days	5/8/2019	3/9/2019							
1523	20.1.15	general site clearance	12 days	4/9/2019	18/9/2019							
1524	20.1.16	initial survey	12 days	19/9/2019	3/10/2019							
1525	20.1.17	utility detection and submit reports	8 days	4/10/2019	14/10/2019							
1526	20.1.18	Fabrication of Steelworks & glass panel	100 days	5/8/2019	2/12/2019							
1527	20.1.19	delivery steelworks & glass panel to site	38 days	3/12/2019	18/1/2020							
1528	20.1.20	application of XP (for Parts D)	0 days	29/11/2018	29/11/2018							
1529	20.1.21	acceptance of XP (for Parts D)	0 days	30/5/2019	30/5/2019							
1530	20.1.22	Construction of Covered Walkway at Fanling Station	390 days	15/10/2019	3/2/2021							
1531	20.1.22.1	construct the concrete foundation of covered walkway (first 20m)	20 days	15/10/2019	6/11/2019							
1532	20.1.22.2	construct the concrete foundation of covered walkway (2nd 20m)	20 days	7/11/2019	29/11/2019							
1533	20.1.22.3	construct the concrete foundation of covered walkway (3rd 20m)	20 days	30/11/2019	23/12/2019							
1534	20.1.22.4	demolished existing planter (drg.WY/1051)	20 days	30/11/2019	23/12/2019							
1535	20.1.22.5	construct the concrete foundation of covered walkway (4th 20m)	20 days	24/12/2019	18/1/2020							
1536	20.1.22.6	construction of covered walkway including steelworks, glass panel and electrical works	265 days	20/1/2020	9/12/2020							
1537	20.1.22.7	Reinstatement of the pavement and street furniture	45 days	10/12/2020	3/2/2021							
1538	20.2	<b>Parts E</b>	782 days	31/5/2018	16/1/2021							
1539	20.2.1	access date for section 3 (Parts E)	0 days	31/5/2018	31/5/2018							
1540	20.2.2	application of XP (for Parts E)	0 days	30/5/2019	30/5/2019							
1541	20.2.3	acceptance of XP (for Parts E)	0 days	28/11/2019	28/11/2019							
1542	20.2.4	Temporary Traffic Arrangement (TTA) Scheme for Sheung Shui Landmark North PTI and Fanling Station Road	242 days	31/5/2019	27/1/2020							
1546	20.2.5	general site clearance	12 days	29/1/2020	11/2/2020							
1547	20.2.6	initial Survey	14 days	12/2/2020	27/2/2020							
1548	20.2.7	utility detection and submit reports	14 days	28/2/2020	14/3/2020							
1549	20.2.8	Road Improvement works at Sheung Shui Landmark North PTI	250 days	16/3/2020	16/1/2021							
1559	21	Planned Completion for section 3 of the works	0 days	3/2/2021	3/2/2021							
1560	22	Completion Date for section 3 of the works	0 days	3/2/2021	3/2/2021							
1561	23	<b>section 4 of the works - Completion of Establishment works for the Landscape Softworks within Parts A1, A2 and B of the Site</b>	1095 days	4/2/2021	3/2/2024							
1562	23.1	Establishment works for the Landscape Softworks within Parts A1, A2 and B of the Site	1095 days	4/2/2021	3/2/2024							
1565	26	<b>section 5 of the works - Completion of Establishment works for the Landscape Softworks within Parts C1 and C2 of the Site</b>	1095 days	4/2/2021	3/2/2024							
1566	26.1	Establishment works for the Landscape Softworks within Parts C1 and C2 of the Site	1095 days	4/2/2021	3/2/2024							
1569	29	<b>section 6 of the works (section Subject to Excision) - Completion of all works within Parts A3 and A4 of the Site except Establishment works. Extent of works under section 6 of the works is defined in Drawing No.:</b>	859 days	28/9/2018	3/2/2021							
1570	29.1	<b>Parts A3</b>	859 days	28/9/2018	3/2/2021							
1571	29.1.1	access date for section 6 (Part A3) - not more than 120 days after the starting date	0 days	28/9/2018	28/9/2018							
1572	29.1.2	The time for ordering the "section Subject to Excision" for section 6 and 7 is within 390 days commencing from and including the starting	0 days	24/6/2019	24/6/2019							



ID	WBS	Task Name	Duration	Start Date	Completion Date	Qtr 4, 2019					Qtr 1, 2023						
						24/9	November 1/7	7/4	June 12/1	18/10	25/7	January 1/5	August 5/2				
1573	29.1.3	form temporary haul road from the south side to Parts A3	5 days	25/6/2019	29/6/2019												
1574	29.1.4	general site clearance & tree felling	12 days	2/7/2019	15/7/2019												
1575	29.1.5	initial survey	12 days	2/7/2019	15/7/2019												
1576	29.1.6	construction of temporary drainage	14 days	15/7/2019	30/7/2019												
1577	29.1.7	<b>Construction of Retaining Wall RW14 (Bay 1-Bay 6)</b>	312 days	26/7/2019	22/8/2020												
1602	29.1.8	backfilling works behind Retaining Wall RW14 (bay1 to 6) (include SRT tests)	90 days	22/8/2020	15/12/2020												
1603	29.1.9	Construction of Retaining Wall RW14 Bay 7	27 days	30/9/2020	9/11/2020												
1613	29.1.10	backfilling works behind RW14 (bay 7) (include SRT tests)	30 days	10/11/2020	15/12/2020												
1614	29.1.11	install instrument for RW14	5 days	11/12/2020	16/12/2020												
1615	29.1.12	construct 300U channel & catchpit in front of R	8 days	11/12/2020	19/12/2020												
1616	29.1.13	site formation works for fill slope FS19 and FS20 (including in "backfilling works behind Retaining Wall RW14 (bay1 to 6)")	90 days	22/8/2020	15/12/2020												
1617	29.1.14	300U channel & stepped channel for FS19 & 2	3 days	16/12/2020	18/12/2020												
1618	29.1.15	install instrument for FS19 & FS20	5 days	16/12/2020	21/12/2020												
1619	29.1.16	minor site formation works for cut slope CS25	1 day	16/12/2020	16/12/2020												
1620	29.1.17	minor site formation works for cut slope CS26	3 days	17/12/2020	19/12/2020												
1621	29.1.18	install instruments for CS25 & CS26	5 days	21/12/2020	28/12/2020												
1622	29.1.19	waterworks at Road E	12 days	21/12/2020	6/1/2021												
1623	29.1.20	drainage works at Road E	10 days	31/12/2020	12/1/2021												
1624	29.1.21	U channels at Road E	7 days	5/1/2021	12/1/2021												
1625	29.1.22	Roadworks of Road E (ch20-60)	19 days	13/1/2021	3/2/2021												
1631	29.1.23	Site Formation works for Cut Slope CS24 (include temporary cutting from top of RW12 to toe of CS24) (for RW12 bays 1-3)	4 days	17/9/2019	20/9/2019												
1632	29.1.24	install instrument for CS24	5 days	23/9/2019	27/9/2019												
1633	29.1.25	temporary soil nails between CS20 & RW12 (for RW12 bays 1-3)	30 days	23/9/2019	4/11/2019												
1634	29.1.26	<b>Construction of Retaining Wall RW12 CH 0-20</b>	67 days	5/11/2019	24/1/2020												
1657	29.1.27	backfilling along Retaining Wall RW12	40 days	4/6/2020	22/7/2020												
1658	29.1.28	Completion of Site Formation works for Cut Slope 25	2 days	21/7/2020	22/7/2020												
1659	29.1.29	Waterworks at Road F	24 days	23/7/2020	19/8/2020												
1660	29.1.30	Drainage works at Road F	25 days	20/8/2020	17/9/2020												
1661	29.1.31	planter wall for Road E and Road F in Parts A3	12 days	18/9/2020	3/10/2020												
1662	29.1.32	UU-Arrange Town Gas & PCCW to lay across Road F (not yet agree)	14 days	5/10/2020	22/10/2020												
1663	29.1.33	Roadworks of Road F (60m)	55 days	23/10/2020	4/1/2021												
1664	29.1.33.1	kerbing and cross road duct (RD/2061, 2081)	10 days	23/10/2020	6/11/2020												
1665	29.1.33.2	ducting for road lighting & construction of irrigation system	12 days	9/11/2020	23/11/2020												
1666	29.1.33.3	bituminous pavement	12 days	24/11/2020	7/12/2020												
1667	29.1.33.4	traffic signs, directional signs, type 2 railing & footpath	21 days	8/12/2020	4/1/2021												
1668	29.1.34	street lighting (Drg/ RD/2091)	6 days	5/1/2021	11/1/2021												
1669	29.1.35	landscaping (hydroseeding)	9 days	12/1/2021	21/1/2021												
1670	29.1.36	landscaping (shrub planting)	11 days	22/1/2021	3/2/2021												
1671	29.2	<b>Parts A4</b>	590 days	24/6/2019	3/2/2021												
1672	29.2.1	access date for section 6 (Parts A4) - not more than 580 days after the starting date	0 days	31/12/2019	31/12/2019												
1673	29.2.2	The time for ordering the "section Subject to Excision" for section 6 and 7 is within 390 days commencing from and including the starting	0 days	24/6/2019	24/6/2019												

ID	WBS	Task Name	Duration	Start Date	Completion Date	Qtr 4, 2019												Qtr 1, 2023											
						November			December			January			February			March			April			May			June		
1674	29.2.3	general site clearance	15 days	2/1/2020	18/1/2020																								
1675	29.2.4	initial survey	11 days	11/1/2020	23/1/2020																								
1676	29.2.5	construction of temporary drainage	15 days	16/1/2020	5/2/2020																								
1677	29.2.6	Site Formation works for Cut Slope CS24 (include temporary cutting from top of RW12 to toe of CS24) (for RW12 bays 4-6)	7 days	29/1/2020	5/2/2020																								
1678	29.2.7	install instrument for CS24	3 days	6/2/2020	8/2/2020																								
1679	29.2.8	temporary soil nails between CS20 & RW12 (for RW12 bays 4-6)	35 days	6/2/2020	17/3/2020																								
1680	29.2.9	Construction of Retaining Wall RW12 CH 21-40	58 days	18/3/2020	3/6/2020																								
1703	29.2.10	Site Formation works for Cut Slope CS20	125 days	1/6/2020	3/11/2020																								
1737	29.2.11	Site Formation works for Cut Slope CS26 (A4)	8 days	13/10/2020	22/10/2020																								
1738	29.2.12	Site Formation works for Cut Slope CS25 (A4)	9 days	23/10/2020	5/11/2020																								
1739	29.2.13	complete the construction of U channel at CS 25 and 26	15 days	4/11/2020	23/11/2020																								
1740	29.2.14	planter wall	10 days	18/11/2020	28/11/2020																								
1741	29.2.15	Waterworks at Road B	8 days	24/11/2020	2/12/2020																								
1742	29.2.16	Sewerage works at Road B	7 days	27/11/2020	4/12/2020																								
1743	29.2.17	Drainage works at Road B	7 days	30/11/2020	7/12/2020																								
1744	29.2.18	UU - Arrange Town Gas & PCCW to lay cables (not agreed yet)	14 days	8/12/2020	23/12/2020																								
1745	29.2.19	Roadworks of Road B (A4-ch90-130)	23 days	23/12/2020	21/1/2021																								
1750	29.2.20	street lighting (Drg/ RD/2091)	4 days	21/1/2021	25/1/2021																								
1751	29.2.21	landscaping (hydroseeding)	7 days	25/1/2021	1/2/2021																								
1752	29.2.22	landscaping (shrub planting)	5 days	29/1/2021	3/2/2021																								
1753	30	Planned Completion for section 6 of the works	0 days	3/2/2021	3/2/2021																								
1754	31	Completion Date for section 6 of the works	0 days	3/2/2021	3/2/2021																								
1755	32	<b>section 7 of the works (section Subject to Excision) - Completion of Establishment works for the Landscape Softworks within Parts A3</b>	1095 days	4/2/2021	3/2/2024																								
1756	32.1	Establishment works for the Landscape Softworks within Parts A3 and A4 of the Site	1095 days	4/2/2021	3/2/2024																								

## **Appendix D**

### **Monitoring Locations**

## **Air Quality Monitoring Location**

Legend


- Project Boundary
- Utilities Construction
- Proposed Air Monitoring Stations

E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15
Rev	Description	By	Date
Consultant			

Contract No. and Title:  
 Agreement No. CE 1/2013(CE)  
 Site Formation and Associated  
 Infrastructural Works for Development  
 of Columbarium, Crematorium and  
 Related Facilities at Sandy Ridge  
 Cemetery - Design and Construction

Drawing title

Copyright Reserved

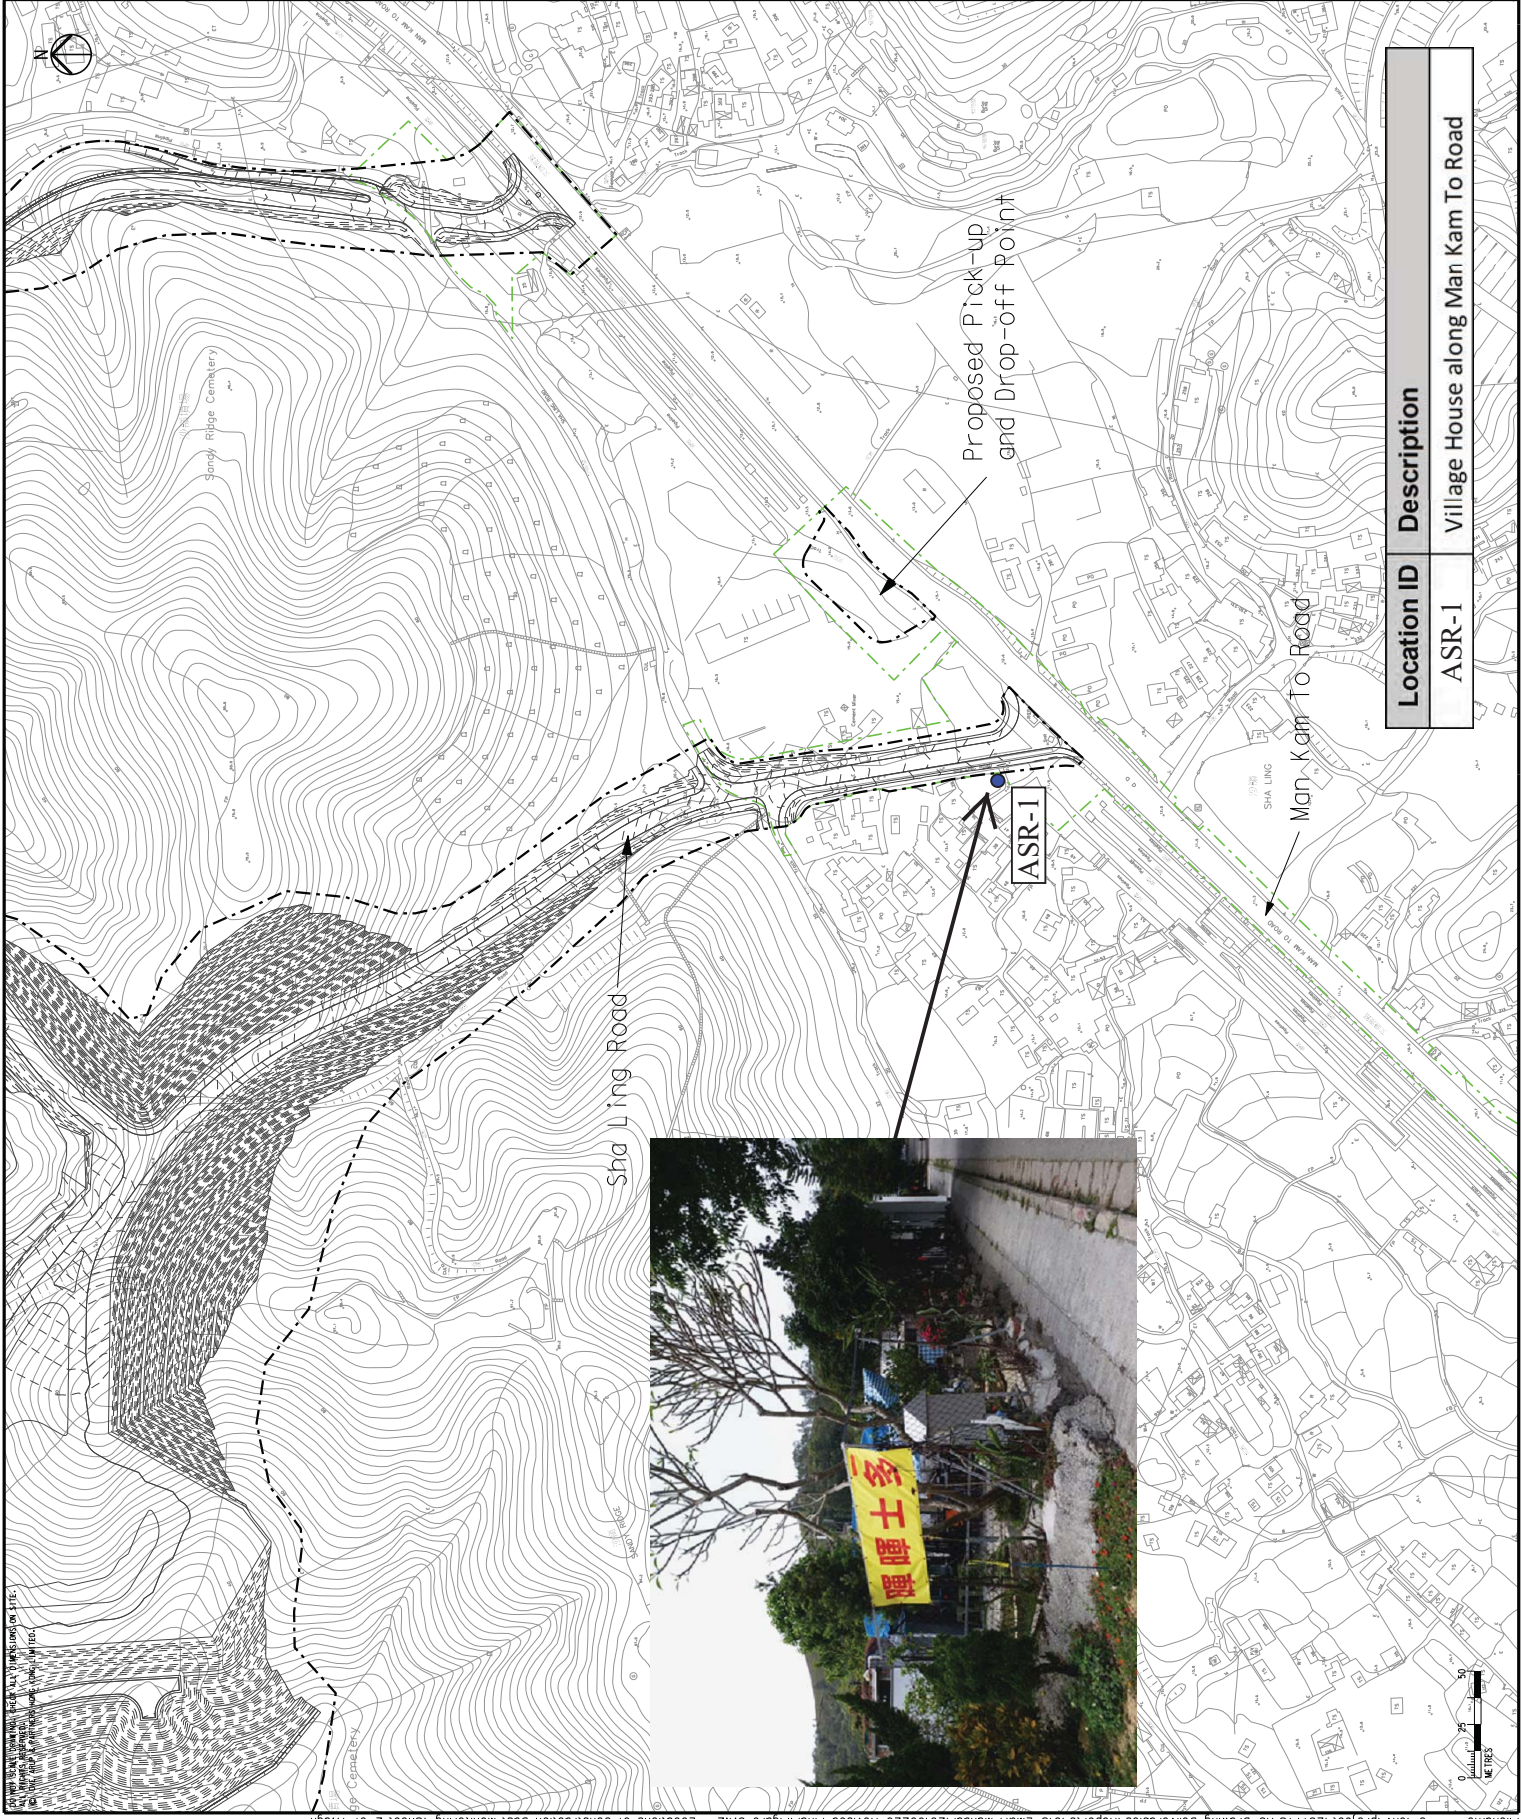

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
 ALL RIGHTS RESERVED.  
 ALL THE RIGHTS PARTIES HAVE ARE RESERVED.

Man Kam To Boundary  
 Control Point



HVS shifted to outside premises of San Uk Ling Village House No.1 for impact air quality monitoring

HVS placed inside premises of San Uk Ling Village House No.1 during baseline air quality monitoring

Location ID	Description
ASR-2	Village House at San Uk Ling

Legend

- Project Boundary
- Existing Air Monitoring Stations

Rev	Description	By	Date
E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15

Contract No. and Title:  
 Agreement No. CE 1/2013(CE)  
 Site Formation and Associated  
 Infrastructural Works for Development  
 of Columbarium, Crematorium and  
 Related Facilities at Sandy Ridge  
 Cemetery - Design and Construction

Drawing title  
**Figure 1**  
**Air Quality Monitoring**  
**Location (ASR-2)**


COPYRIGHT RESERVED



Location ASR-3 at Muk Wu Nga Yiu House No. 28 during baseline monitoring



Proposed Location ASR-3a at Muk Wu Nga Yiu House No. 2A for impact monitoring

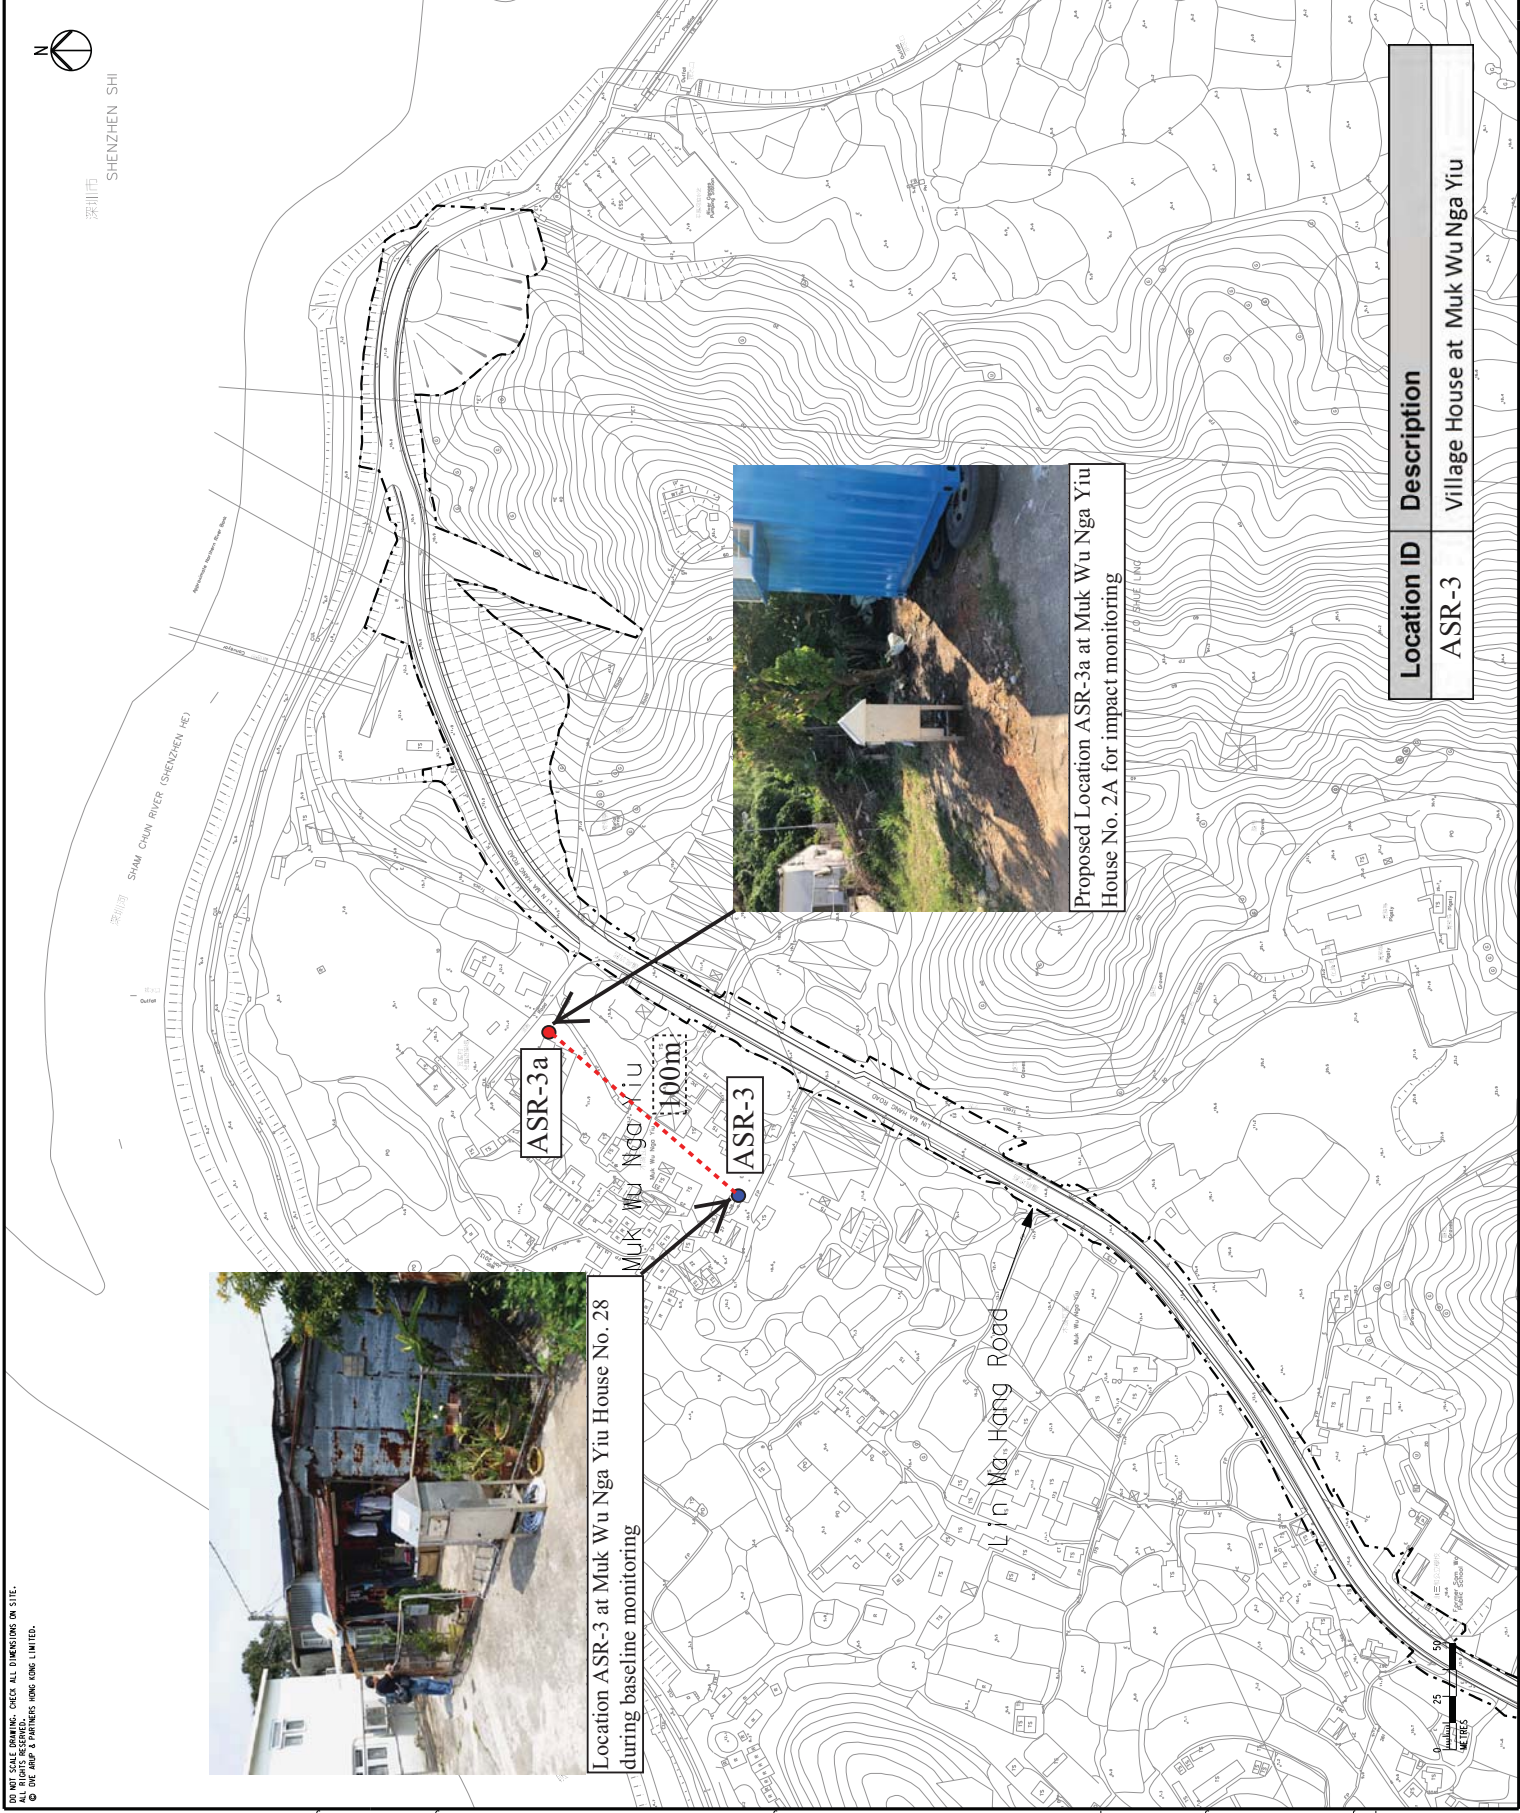

Location ID	Description
ASR-3	Village House at Muk Wu Nga Yiu

Legend

- Project Boundary
- Existing Air Monitoring Station
- Proposed Air Monitoring Station


Rev	Description	By	Date
E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15

Contract No. and Title:  
 Agreement No. CE 1/2013(CE)  
 Site Formation and Associated  
 Infrastructural Works for Development  
 of Columbarium, Crematorium and  
 Related Facilities at Sandy Ridge  
 Cemetery - Design and Construction

Drawing title:  
**Figure 2**  
**Air Quality Monitoring**  
**Location (ASR-3)**

## **Noise Monitoring Location**



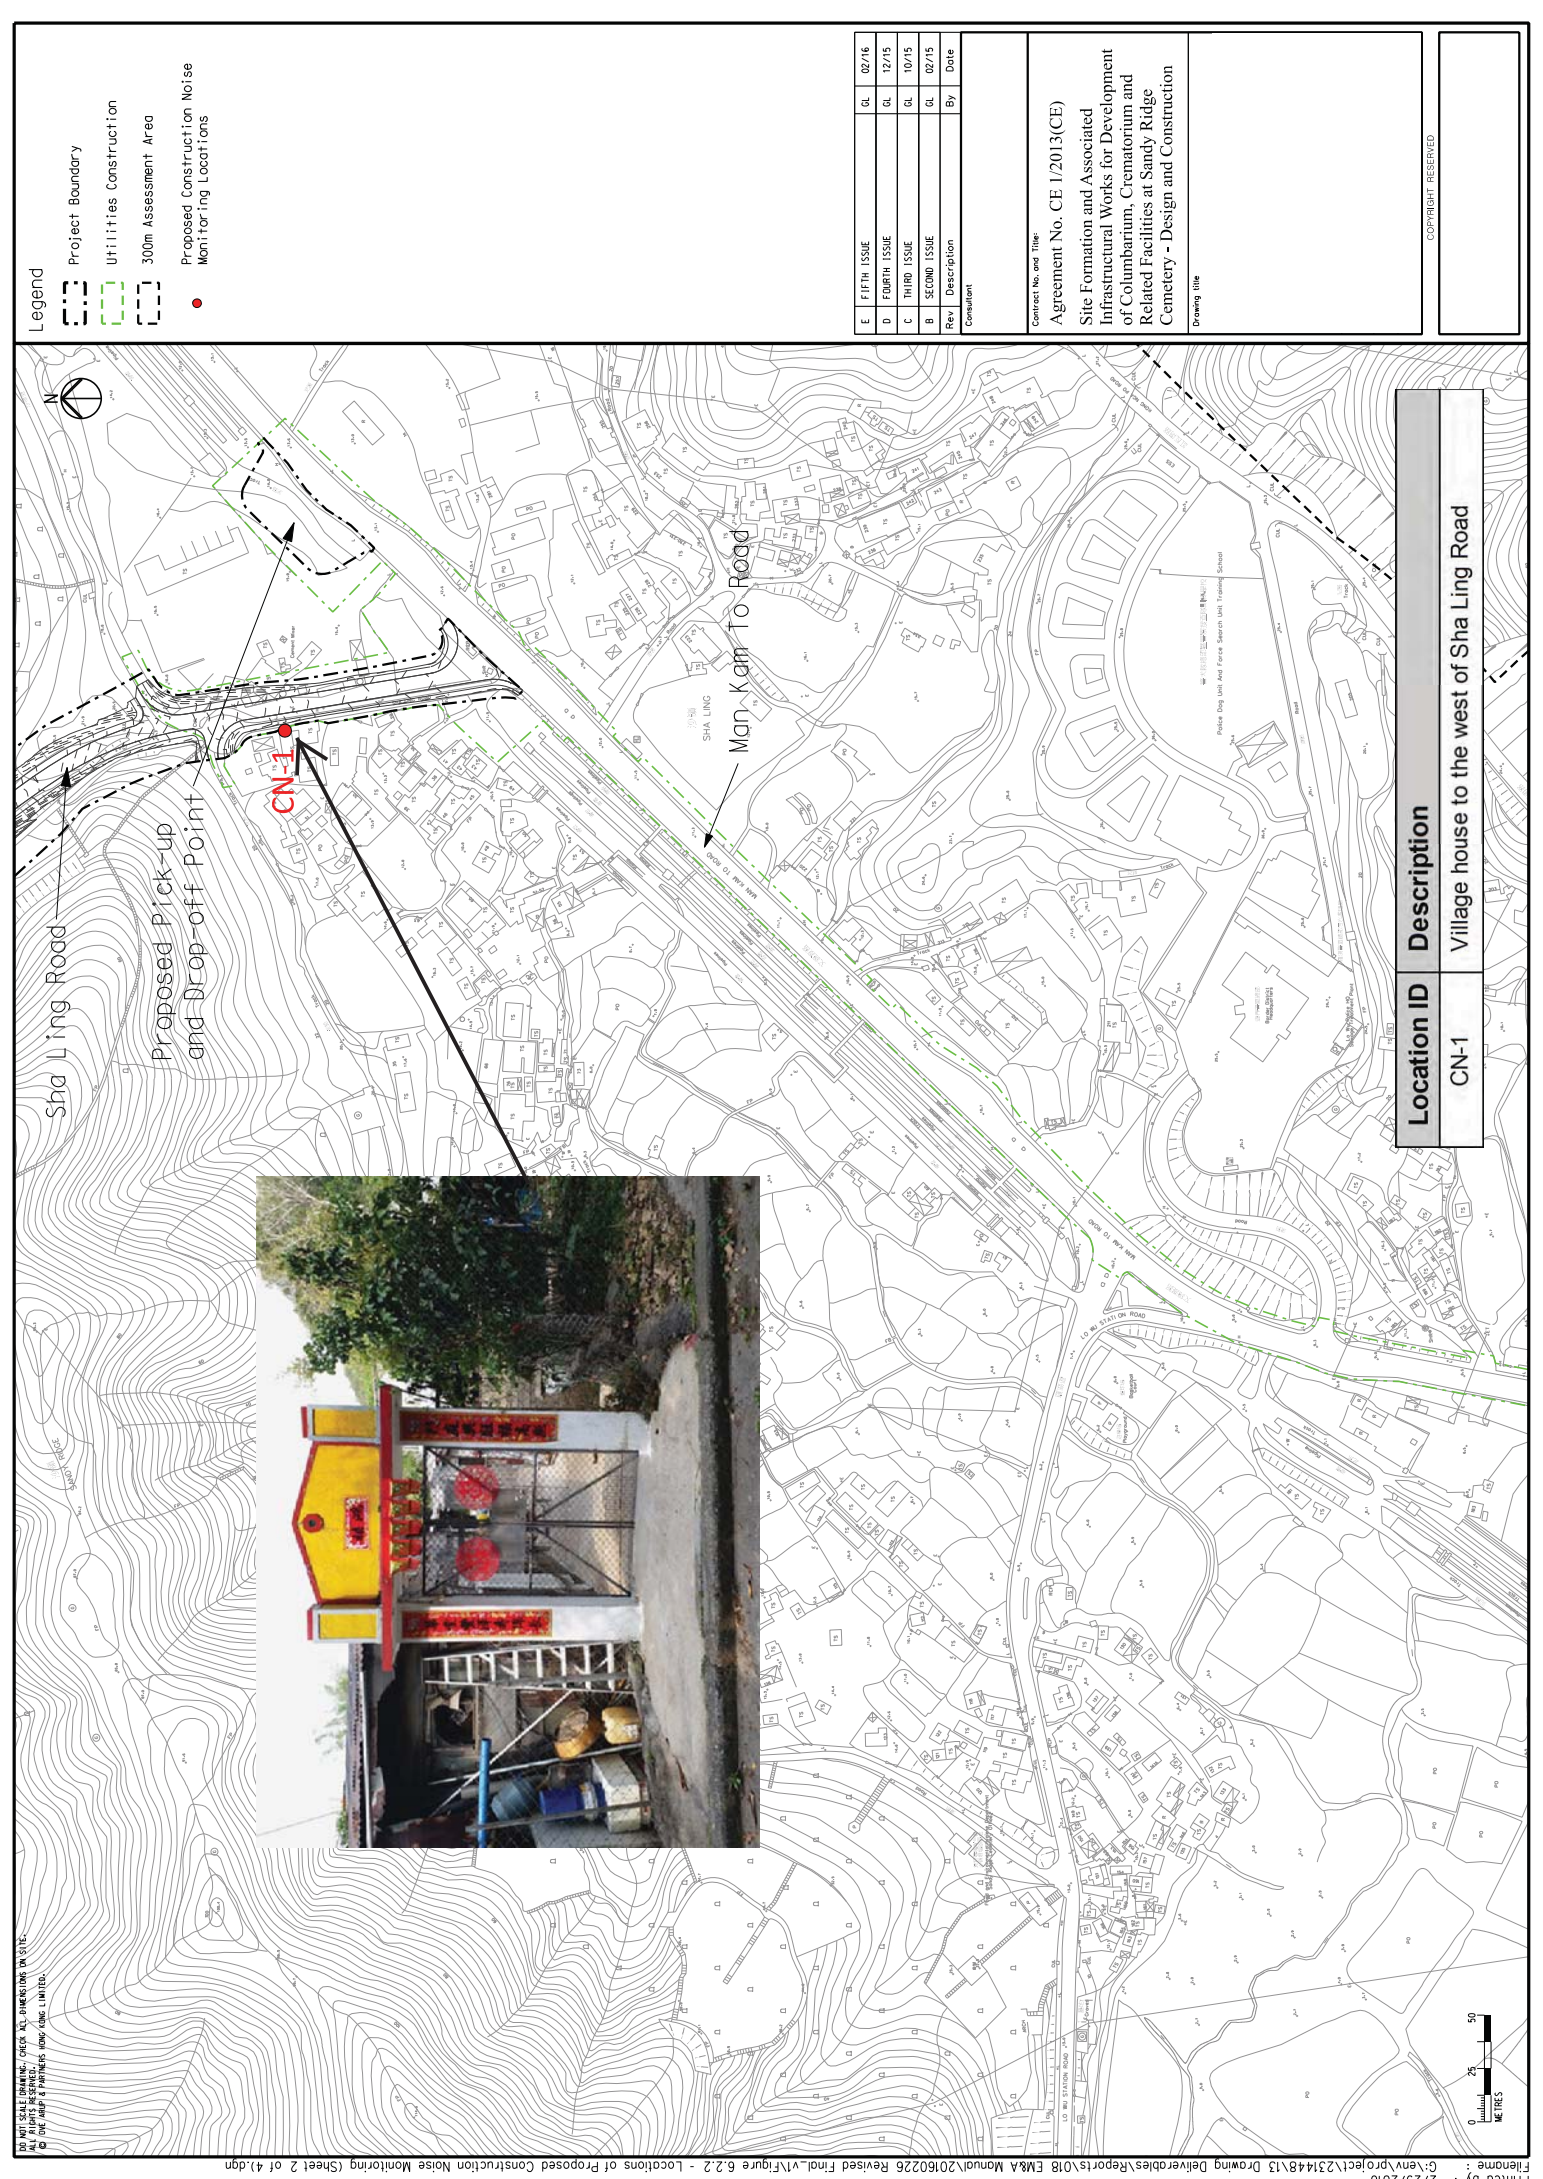

Location ID	Description
CN-1	Village house to the west of Sha Ling Road

- Legend**
- Project Boundary
  - Utilities Construction
  - 300m Assessment Area
  - Proposed Construction Noise Monitoring Locations

Rev	Description	By	Date
E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15

Contract No. and Title:  
 Agreement No. CE 1/2013(CE)  
 Site Formation and Associated  
 Infrastructural Works for Development  
 of Columbarium, Crematorium and  
 Related Facilities at Sandy Ridge  
 Cemetery - Design and Construction

Drawing title

COPYRIGHT RESERVED



**Legend**

- Project Boundary
- Utilities Construction
- 300m Assessment Area
- Proposed Construction Noise Monitoring Locations



E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15
Rev	Description	By	Date
Consultant			
Contract No. and Title: Agreement No. CE 1/2013(CE) Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery - Design and Construction			
Drawing title			
Copyright Reserved			

2018/4/6

Location ID	Description
CN-2	Village house to the north of Man Kam To Road

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
 ALL RIGHTS RESERVED.  
 © THE SHIP & PARTNERS INC. (UK) LIMITED.



**Legend**

- Project Boundary
- 300m Assessment Area
- Proposed Construction Noise Monitoring Locations

Rev	Description	By	Date
E	FIFTH ISSUE	GL	02/16
D	FOURTH ISSUE	GL	12/15
C	THIRD ISSUE	GL	10/15
B	SECOND ISSUE	GL	02/15

Consultant

Contract No. and Title:  
**Agreement No. CE 1/2013(CE)**  
**Site Formation and Associated**  
**Infrastructural Works for Development**  
**of Columbarium, Crematorium and**  
**Related Facilities at Sandy Ridge**  
**Cemetery - Design and Construction**

Drawing Title

COPYRIGHT RESERVED

Location ID	Description
CN-3	Village house near San Uk Ling
CN-4	Village house of Muk Wu

## **Water Quality Monitoring Station**



**Legend**

- Project Boundary
- Utilities Construction
- 500m Assessment Area
- Channelized River
- Pond
- Watercourse
- Conservation Area (CA)
- Wet Woodland
- Seasonal Watercourse
- Base line Monitoring Station



Rev	Description	By	Date
B	SECOND ISSUE	GL	02/15
C	THIRD ISSUE	GL	10/15
D	FOURTH ISSUE	GL	12/15
E	FIFTH ISSUE	GL	02/16

Consultant  
**ARUP**

Contract No. and Title:  
 Agreement No. CE 1/2013(CE)  
 Site Formation and Associated  
 Infrastructural Works for Development  
 of Columbarium, Crematorium and  
 Related Facilities at Sandy Ridge  
 Cemetery - Design and Construction

Drawing title  
**Water Quality Monitoring  
 Locations**

Drawing no.	Figure 7.1.1		Rev.	E
Drawn	Date	Checked	Approved	
Scale	AS SHOWN	Status	PRELIMINARY	

Copyright Reserved  
  
 土木工程拓展署  
 Civil Engineering and  
 Development Department

## **Appendix E**

# **Calibration Certificate of Monitoring Equipment and Laboratory Certificate**

**CALIBRATION CERTIFICATES FOR MONITORING EQUIPMENT USED IN THE REPORTING MONTH**

Items	Aspect	Description of Equipment	Date of Calibration	Date of Next Calibration
1a	Air	TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-1	20 Jan 23	3 Feb 23
1b		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-1	7 Feb 23	21 Feb 23
1c		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-1	24 Feb 23	10 Mar 23
2		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-2	20 Jan 23	3 Feb 23
2a		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-2	7 Feb 23	21 Feb 23
2b		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-2	24 Feb 23	10 Mar 23
3		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-3a	20 Jan 23	3 Feb 23
3a		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-3a	7 Feb 23	21 Feb 23
3b		TISCH High Volume Air Sampler, HVS Model TE-5170 TSP Sampler Calibration Spreadsheet for ASR-3a	24 Feb 23	10 Mar 23
4		Calibration Kit TISCH Model TE-5025A Orifice ID 4064 and Rootsmeter S/N 438320	15 Dec 22	15 Dec 23
5		Laser Dust Monitor, Model LD-3B (Serial No. 3Y6502) – EQ113	26 Mar 22	26 Mar 23
6		Laser Dust Monitor, Model LD-3B (Serial No. 3Y6505) – EQ114	26 Mar 22	26 Mar 23
7		Laser Dust Monitor, Model LD-3B (Serial No. 456658) – EQ115	26 Mar 22	26 Mar 23
9	Noise	Rion NL-52 Sound Level Meter (Serial No. 00809405) – EQ018	12 Mar 22	12 Mar 23
10		Rion NL-31 Sound Level Meter (Serial No. 00410221) – EQ067	12 Mar 22	12 Mar 23
11		Rion NC-73 Acoustical Calibrator (Serial No. 10655561) – EQ085	20 Aug 22	20 Aug 23
12	Water	YSI Professional DSS (Serial No.17B102764)	4 Jan 23	4 Apr 23
13		Global Water FP211 Flow Meter (Serial No. 22B106785)	3 May 22	3 May 23

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Sha Ling Village House No.6

Date of Calibration: 20-Jan-23

Location ID : ASR-1

Next Calibration Date: 3-Feb-23

Name and Model: TISCH HVS Model TE-5170

Technician: Eric Chan

### CONDITIONS

Sea Level Pressure (hPa) 1021.4  
 Temperature (°C) 17.6

Corrected Pressure (mm Hg) 766.05  
 Temperature (K) 291

### CALIBRATION ORIFICE

Make-> TISCH  
 Model-> 5025A  
 Serial # -> 4064

Qstd Slope -> 2.10977  
 Qstd Intercept -> -0.03782

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.50	6.50	13.0	1.755	55	56.62	Slope = 32.0664 Intercept = 0.8645 Corr. coeff. = 0.9992
13	5.40	5.40	10.8	1.602	51	52.51	
10	4.30	4.30	8.6	1.431	46	47.36	
7	2.70	2.70	5.4	1.138	36	37.06	
5	1.70	1.70	3.4	0.906	29	29.86	

**Calculations :**

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

**FLOW RATE CHART**

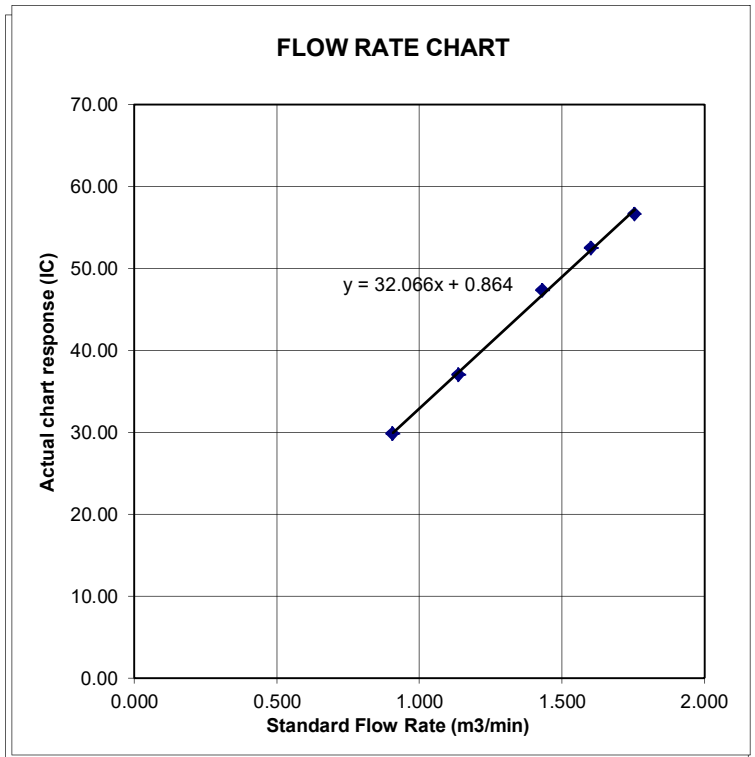



## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : San Uk Ling Village House No.1

Date of Calibration: 20-Jan-23

Location ID : ASR-2

Next Calibration Date: 3-Feb-23

Name and Model: TISCH HVS Model TE-5170

Technician: Eric Chan

### CONDITIONS

Sea Level Pressure (hPa) 1021.4  
 Temperature (°C) 17.6

Corrected Pressure (mm Hg) 766.05  
 Temperature (K) 291

### CALIBRATION ORIFICE

Make-> TISCH  
 Model-> 5025A  
 Serial # -> 4064

Qstd Slope -> 2.10977  
 Qstd Intercept -> -0.03782

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.50	6.50	13.0	1.755	56	57.65	Slope = 32.9140 Intercept = -0.6622 Corr. coeff. = 0.9990
13	5.50	5.50	11.0	1.616	51	52.51	
10	4.40	4.40	8.8	1.447	45	46.33	
7	2.50	2.50	5.0	1.095	34	35.00	
5	1.60	1.60	3.2	0.880	28	28.83	

**Calculations :**

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

**FLOW RATE CHART**

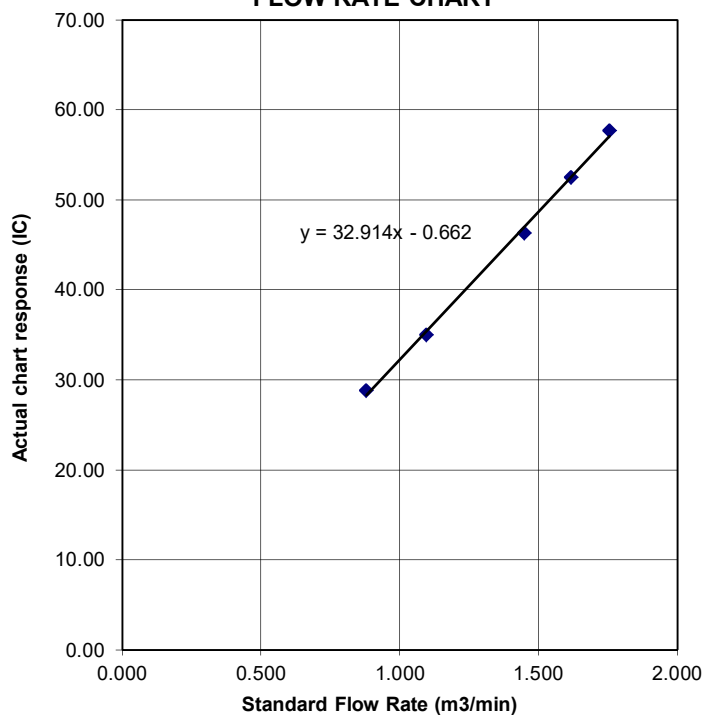

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Muk Wu Nga Yiu House No.2A	Date of Calibration: 20-Jan-23
Location ID : ASR-3a	Next Calibration Date: 3-Feb-23
Name and Model: TISCH HVS Model TE-5170	Technician: Eric Chan

### CONDITIONS

Sea Level Pressure (hPa)	1021.4	Corrected Pressure (mm Hg)	766.05
Temperature (°C)	17.6	Temperature (K)	291

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.10977
Model->	5025A	Qstd Intercept ->	-0.03782
Serial # ->	4064		

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
							Slope = 32.3320
18	6.50	6.50	13.0	1.755	55	56.62	Intercept = -0.5894 Corr. coeff. = 0.9970
13	5.30	5.30	10.6	1.587	50	51.48	
10	4.30	4.30	8.6	1.431	43	44.27	
7	2.60	2.60	5.2	1.117	34	35.00	
5	1.40	1.40	2.8	0.824	26	26.77	

#### Calculations :

$$Qstd = 1/m[\text{Sqrt}(H20(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

#### For subsequent calculation of sampler flow:

$$1/m(( I )[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

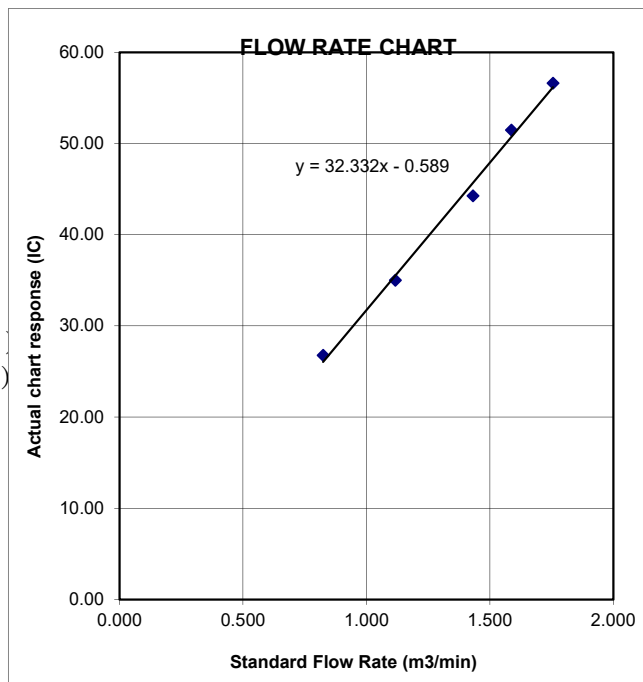

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Sha Ling Village House No.6

Date of Calibration: 7 Feb 23

Location ID : ASR-1

Next Calibration Date: 21 Feb 23

Name and Model: TISCH HVS Model TE-5170

Technician: Eric Chan

### CONDITIONS

Sea Level Pressure (hPa) 1015.4  
 Temperature (°C) 21.0

Corrected Pressure (mm Hg) 761.55  
 Temperature (K) 294

### CALIBRATION ORIFICE

Make-> TISCH  
 Model-> 5025A  
 Serial # -> 4064

Qstd Slope -> 2.10977  
 Qstd Intercept -> -0.03782

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.50	6.50	13.0	1.740	56	56.82	Slope = 33.2025 Intercept = -1.0090 Corr. coeff. = 0.9991
13	5.40	5.40	10.8	1.588	51	51.75	
10	4.30	4.30	8.6	1.419	45	45.66	
7	2.60	2.60	5.2	1.107	36	36.53	
5	1.70	1.70	3.4	0.899	28	28.41	

**Calculations :**

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

**FLOW RATE CHART**

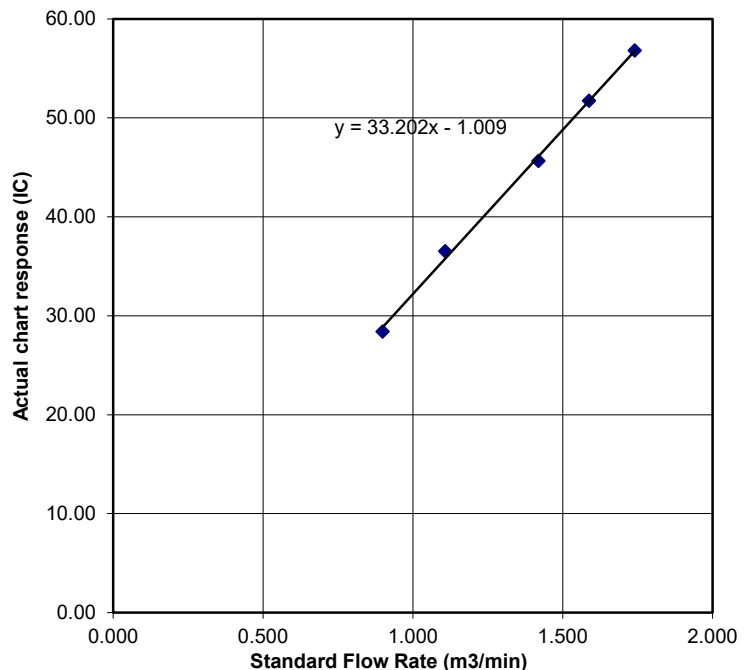

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : San Uk Ling Village House No.1  
 Location ID : ASR-2  
 Name and Model: TISCH HVS Model TE-5170

Date of Calibration: 7 Feb 23  
 Next Calibration Date: 21 Feb 23  
 Technician: Eric Chan

### CONDITIONS

Sea Level Pressure (hPa) 1015.4  
 Temperature (°C) 21.0

Corrected Pressure (mm Hg) 761.55  
 Temperature (K) 294

### CALIBRATION ORIFICE

Make-> TISCH  
 Model-> 5025A  
 Serial # -> 4064

Qstd Slope -> 2.10977  
 Qstd Intercept -> -0.03782

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.50	6.50	13.0	1.740	56	56.82	Slope = 33.9677 Intercept = -1.9231 Corr. coeff. = 0.9988
13	5.40	5.40	10.8	1.588	52	52.76	
10	4.30	4.30	8.6	1.419	45	45.66	
7	2.50	2.50	5.0	1.086	35	35.51	
5	1.60	1.60	3.2	0.872	27	27.40	

**Calculations :**

$$Q_{std} = 1/m[\sqrt{H2O(P_a/P_{std})(T_{std}/T_a)} - b]$$

$$IC = I[\sqrt{P_a/P_{std}}(T_{std}/T_a)]$$


Qstd = standard flow rate  
 IC = corrected chart responses  
 I = actual chart response  
 m = calibrator Qstd slope  
 b = calibrator Qstd intercept  
 Ta = actual temperature during calibration ( deg K )  
 Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\sqrt{298/T_{av}}(P_{av}/760)] - b)$$

m = sampler slope  
 b = sampler intercept  
 I = chart response  
 Tav = daily average temperature  
 Pav = daily average pressure

**FLOW RATE CHART**

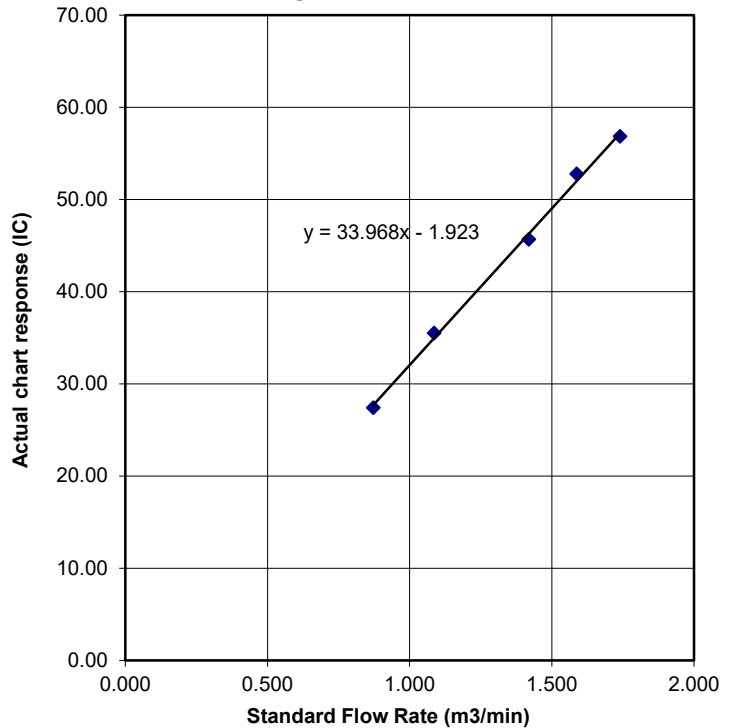

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Muk Wu Nga Yiu House No.2A	Date of Calibration: 7 Feb 23
Location ID : ASR-3a	Next Calibration Date: 21 Feb 23
Name and Model: TISCH HVS Model TE-5170	Technician: Eric Chan

### CONDITIONS

Sea Level Pressure (hPa) <span style="float: right;">1015.4</span>	Corrected Pressure (mm Hg) <span style="float: right;">761.55</span>
Temperature (°C) <span style="float: right;">21.0</span>	Temperature (K) <span style="float: right;">294</span>

### CALIBRATION ORIFICE

Make-> TISCH	Qstd Slope -> 2.10977
Model-> 5025A	Qstd Intercept -> -0.03782
Serial # -> 4064	

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
							Slope = 32.2726
18	6.50	6.50	13.0	1.740	55	55.81	Intercept = -0.7142
13	5.40	5.40	10.8	1.588	50	50.73	Corr. coeff. = 0.9986
10	4.30	4.30	8.6	1.419	44	44.64	
7	2.50	2.50	5.0	1.086	33	33.48	
5	1.40	1.40	2.8	0.817	26	26.38	

#### Calculations :

$$Qstd = 1/m[\text{Sqrt}(H20(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

#### For subsequent calculation of sampler flow:

$$1/m(( I )[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

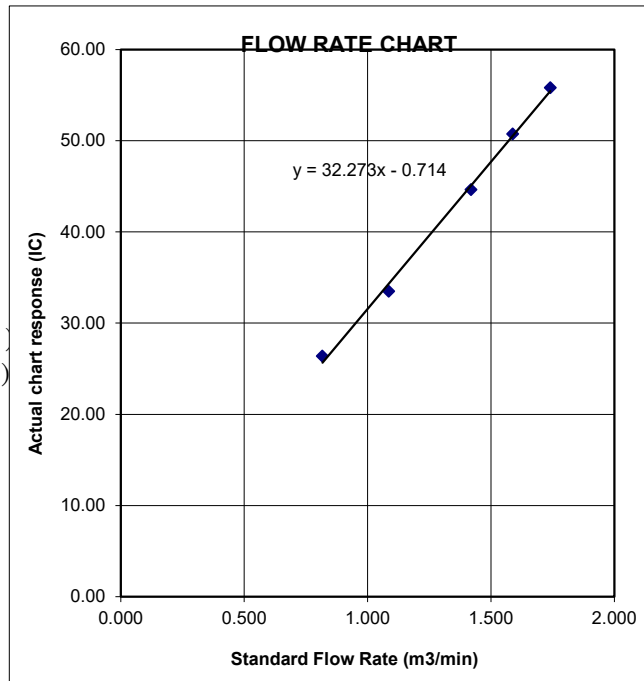

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Sha Ling Village House No.6

Date of Calibration: 24 Feb 23

Location ID : ASR-1

Next Calibration Date: 10 Mar 23

Name and Model: TISCH HVS Model TE-5170

Technician: Eric Chan

### CONDITIONS

Sea Level Pressure (hPa) 1018.9  
 Temperature (°C) 19.8

Corrected Pressure (mm Hg) 764.175  
 Temperature (K) 293

### CALIBRATION ORIFICE

Make-> TISCH  
 Model-> 5025A  
 Serial # -> 4064

Qstd Slope -> 2.10977  
 Qstd Intercept -> -0.03782

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.50	6.50	13.0	1.747	58	59.19	Slope = 38.8351 Intercept = -9.0146 Corr. coeff. = 0.9974
13	5.20	5.20	10.4	1.564	51	52.05	
10	4.30	4.30	8.6	1.424	44	44.90	
7	2.40	2.40	4.8	1.068	33	33.68	
5	1.70	1.70	3.4	0.902	25	25.51	

**Calculations :**

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

**FLOW RATE CHART**

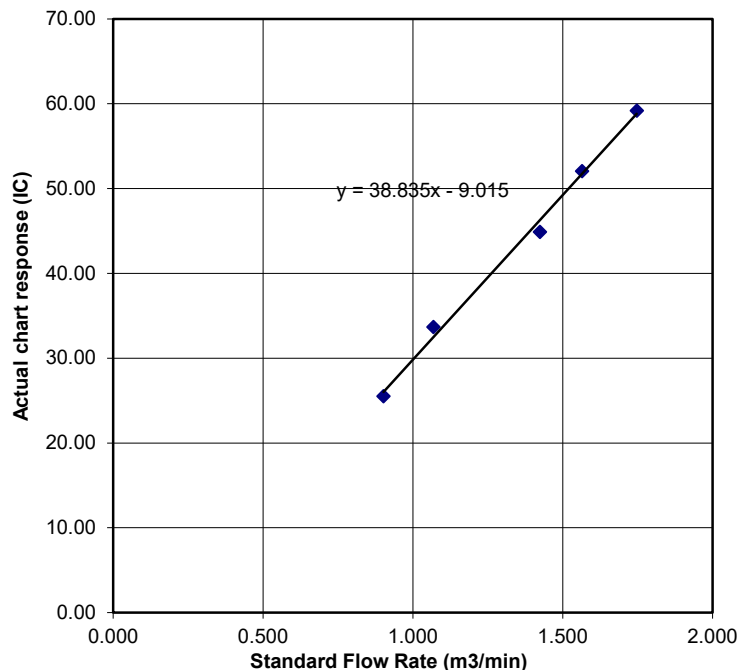

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : San Uk Ling Village House No.1  
 Location ID : ASR-2  
 Name and Model: TISCH HVS Model TE-5170

Date of Calibration: 24 Feb 23  
 Next Calibration Date: 10 Mar 23  
 Technician: Eric Chan

### CONDITIONS

Sea Level Pressure (hPa) 1018.9  
 Temperature (°C) 19.8

Corrected Pressure (mm Hg) 764.175  
 Temperature (K) 293

### CALIBRATION ORIFICE

Make-> TISCH  
 Model-> 5025A  
 Serial # -> 4064

Qstd Slope -> 2.10977  
 Qstd Intercept -> -0.03782

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.50	6.50	13.0	1.747	58	59.19	Slope = 35.1845 Intercept = -2.6598 Corr. coeff. = 0.9976
13	5.40	5.40	10.8	1.594	53	54.09	
10	4.30	4.30	8.6	1.424	45	45.92	
7	2.50	2.50	5.0	1.090	35	35.72	
5	1.60	1.60	3.2	0.876	28	28.58	

**Calculations :**

$$Q_{std} = 1/m[\text{Sqrt}(H2O(Pa/P_{std})(T_{std}/T_a))-b]$$

$$IC = I[\text{Sqrt}(Pa/P_{std})(T_{std}/T_a)]$$


Qstd = standard flow rate  
 IC = corrected chart responses  
 I = actual chart response  
 m = calibrator Qstd slope  
 b = calibrator Qstd intercept  
 Ta = actual temperature during calibration ( deg K )  
 Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\text{Sqrt}(298/T_{av})(P_{av}/760)]-b)$$

m = sampler slope  
 b = sampler intercept  
 I = chart response  
 Tav = daily average temperature  
 Pav = daily average pressure

**FLOW RATE CHART**

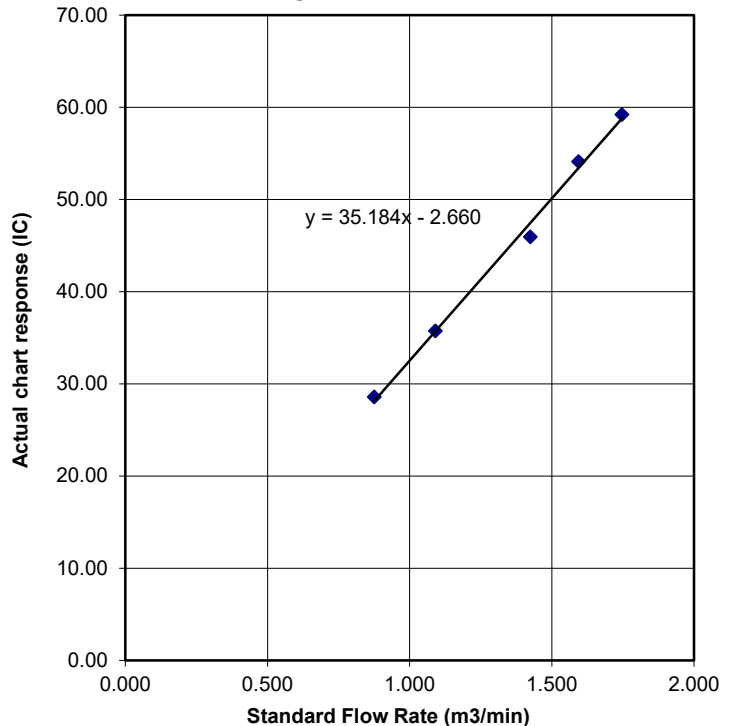

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Muk Wu Nga Yiu House No.2A                      Date of Calibration: 24 Feb 23  
 Location ID : ASR-3a    Next Calibration Date: 10 Mar 23  
 Name and Model: TISCH HVS Model TE-5170                      Technician: Eric Chan

CONDITIONS			
Sea Level Pressure (hPa)	1018.9	Corrected Pressure (mm Hg)	764.175
Temperature (°C)	19.8	Temperature (K)	293

CALIBRATION ORIFICE			
Make->	TISCH	Qstd Slope ->	2.10977
Model->	5025A	Qstd Intercept ->	-0.03782
Serial # ->	4064		


CALIBRATION							
Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.50	6.50	13.0	1.747	55	56.13	Slope = 32.1255 Intercept = -0.8271 Corr. coeff. = 0.9973
13	5.30	5.30	10.6	1.579	49	50.01	
10	4.30	4.30	8.6	1.424	43	43.88	
7	2.40	2.40	4.8	1.068	32	32.66	
5	1.30	1.30	2.6	0.791	25	25.51	

**Calculations :**

$Q_{std} = 1/m[\text{Sqrt}(H2O(Pa/P_{std})(T_{std}/T_a))-b]$   
 $IC = I[\text{Sqrt}(Pa/P_{std})(T_{std}/T_a)]$   
  
 Qstd = standard flow rate  
 IC = corrected chart responses  
 I = actual chart response  
 m = calibrator Qstd slope  
 b = calibrator Qstd intercept  
 Ta = actual temperature during calibration ( deg K )  
 Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$1/m(( I )[\text{Sqrt}(298/T_{av})(P_{av}/760)]-b)$   
  
 m = sampler slope  
 b = sampler intercept  
 I = chart response  
 Tav = daily average temperature  
 Pav = daily average pressure

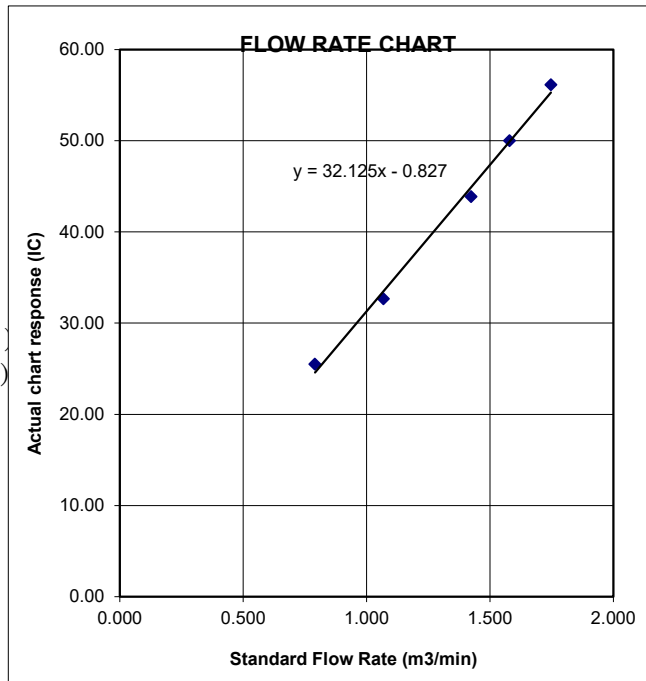





## ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

### SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: <b>HK2214745</b>
CLIENT	: <b>ACTION-UNITED ENVIRONMENTAL SERVICES &amp; CONSULTING</b>		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T.	SUB-BATCH	: 1
		DATE RECEIVED	: 12-APR-2022
		DATE OF ISSUE	: 29-APR-2022
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

#### General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action United Environmental Services & Consulting.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

*Signatories*

*Position*

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

**ALS Technichem (HK) Pty Ltd**  
Part of the **ALS Laboratory Group**

11/F. Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong  
Tel. +852 2610 1044 Fax. +852 2610 2021 [www.alsglobal.com](http://www.alsglobal.com)

WORK ORDER : HK2214745  
SUB-BATCH : 1  
CLIENT : ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING  
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2214745-001	S/N: 3Y6502	AIR	12-Apr-2022	S/N: 3Y6502

## Equipment Verification Report (TSP)

### Equipment Calibrated:

Type: Laser Dust monitor  
 Manufacturer: Sibata LD-3B  
 Serial No. 3Y6502  
 Equipment Ref: EQ113

### Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)  
 Location & Location ID: AUES office (calibration room)  
 Equipment Ref: HVS 018 & HVS 019  
 Last Calibration Date: 22 February 2022

### Equipment Verification Results:

Verification Date: 1 & 7 March 2022

Date	Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in ug/m <sup>3</sup> (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
7-Mar-22	2hr01mins	09:17 ~ 11:18	22.5	1010.6	26.4	947	7.9
7-Mar-22	2hr01mins	11:24 ~ 13:25	22.5	1010.6	34.8	1449	12.0
7-Mar-22	2hr01mins	13:30 ~ 15:31	22.5	1010.6	40.3	1874	15.5
1-Mar-22	30mins	10:03 ~ 10:33	22	1016.9	123.1	1709	57.0
1-Mar-22	31mins	10:39 ~ 11:10	22	1016.9	93.9	1401	45.8

(\* Suspended particle was added into calibration room of HVS019 for high concentration test.

Sensitivity Adjustment Scale Setting (Before Calibration) 655 (CPM)


Sensitivity Adjustment Scale Setting (After Calibration) 661 (CPM)

### Linear Regression of Y or X

Slope (K-factor): 2.0049 (ug/m<sup>3</sup>)/CPM

Correlation Coefficient (R) 0.9948

Date of Issue 26 March 2022

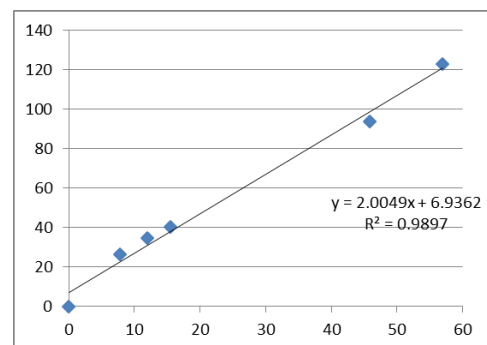

### Remarks:

1. **Strong** Correlation (R>0.8)
2. Factor 2.0049 (ug/m<sup>3</sup>)/CPM should be apply for TSP monitoring

\*If R<0.5, repair or re-verification is required for the equipment

Operator : Fai So Signature :  Date : 26 March 2022

QC Reviewer : Ben Tam Signature :  Date : 26 March 2022

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Kwai Chung Date of Calibration: 22-Feb-22  
 Location ID : Calibration Room Next Calibration Date: 22-May-22

### CONDITIONS

Sea Level Pressure (hPa)	1010.8	Corrected Pressure (mm Hg)	758.1
Temperature (°C)	22.8	Temperature (K)	296

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	1.99838
Model->	5025A	Qstd Intercept ->	-0.00903
Calibration Date->	27-Dec-21	Expiry Date->	27-Dec-22

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.8	5.8	11.6	1.713	54	54.13	Slope = 27.3242 Intercept = 7.2177 Corr. coeff. = 0.9997
13	4.7	4.7	9.4	1.543	49	49.12	
10	3.6	3.6	7.2	1.351	44	44.11	
8	2.3	2.3	4.6	1.080	37	37.09	
5	1.4	1.4	2.8	0.844	30	30.07	

**Calculations :**

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate  
 IC = corrected chart responses  
 I = actual chart response  
 m = calibrator Qstd slope  
 b = calibrator Qstd intercept  
 Ta = actual temperature during calibration ( deg K )  
 Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope  
 b = sampler intercept  
 I = chart response  
 Tav = daily average temperature  
 Pav = daily average pressure

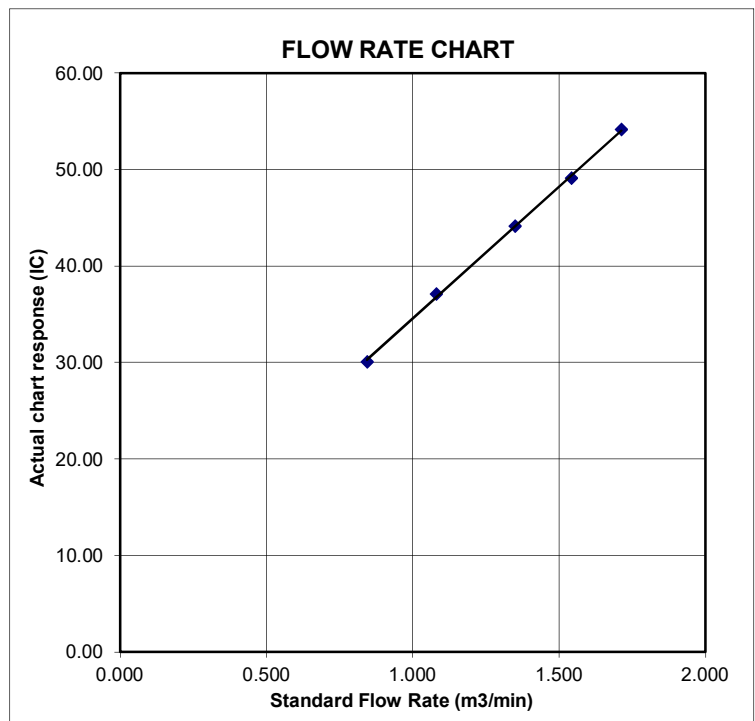

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Kwai Chung Date of Calibration: 22-Feb-22  
 Location ID : Calibration Room Next Calibration Date: 22-May-22

### CONDITIONS

Sea Level Pressure (hPa)	1010.8	Corrected Pressure (mm Hg)	758.1
Temperature (°C)	22.8	Temperature (K)	296

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	1.99838
Model->	5025A	Qstd Intercept ->	-0.00903
Calibration Date->	27-Dec-21	Expiry Date->	27-Dec-22

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.771	52	52.13	Slope = 34.6002 Intercept = -9.1434 Corr. coeff. = 0.9958
13	4.9	4.9	9.8	1.575	44	44.11	
10	3.8	3.8	7.6	1.387	40	40.10	
8	2.4	2.4	4.8	1.104	30	30.07	
5	1.5	1.5	3.0	0.873	20	20.05	

**Calculations :**

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration ( deg K )

Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

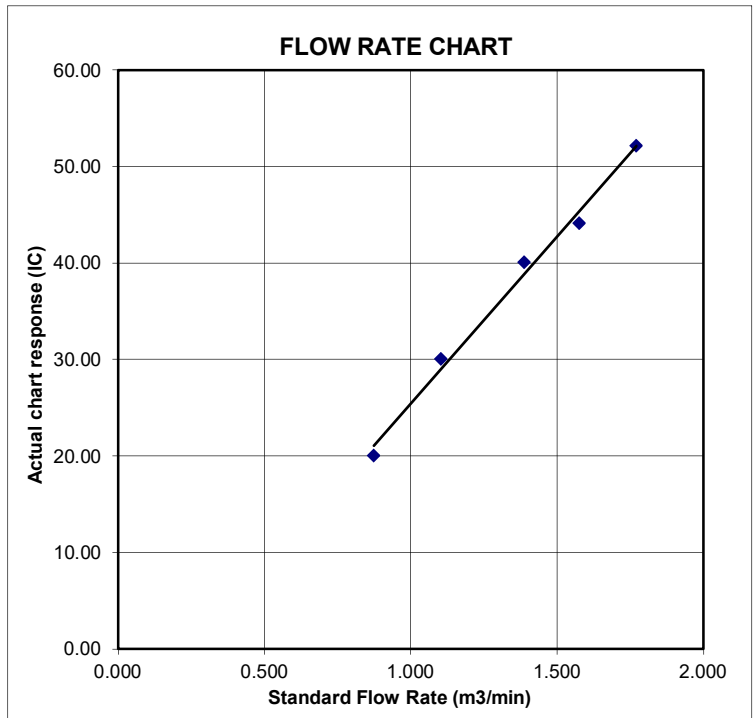



# Certificate of Calibration

Calibration Certification Information			
Cal. Date: December 27, 2021	Rootsmeter S/N: 438320	Ta: 295	°K
Operator: Jim Tisch		Pa: 740.4	mm Hg
Calibration Model #: TE-5025A	Calibrator S/N: <b>1612</b>		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3890	3.2	2.00
2	3	4	1	0.9760	6.4	4.00
3	5	6	1	0.8740	7.9	5.00
4	7	8	1	0.8320	8.8	5.50
5	9	10	1	0.6870	12.7	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left( \frac{Ta}{Pa} \right)}$ (y-axis)
0.9799	0.7055	1.4029	0.9957	0.7168	0.8927
0.9756	0.9996	1.9841	0.9914	1.0157	1.2624
0.9736	1.1140	2.2183	0.9893	1.1320	1.4114
0.9724	1.1688	2.3265	0.9881	1.1876	1.4803
0.9673	1.4079	2.8059	0.9828	1.4306	1.7853
<b>QSTD</b>	m=	<b>1.99838</b>	<b>QA</b>	m=	<b>1.25135</b>
	b=	<b>-0.00903</b>		b=	<b>-0.00574</b>
	r=	<b>0.99999</b>		r=	<b>0.99999</b>

Calculations			
Vstd=	$\Delta Vol \left( \frac{Pa - \Delta P}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)$	Va=	$\Delta Vol \left( \frac{Pa - \Delta P}{Pa} \right)$
Qstd=	Vstd/ΔTime	Qa=	Va/ΔTime
For subsequent flow rate calculations:			
Qstd=	$1/m \left( \left( \sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa=	$1/m \left( \left( \sqrt{\Delta H \left( \frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30



## ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

### SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: <b>HK2212152</b>
CLIENT	: <b>ACTION-UNITED ENVIRONMENTAL SERVICES &amp; CONSULTING</b>		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T.	SUB-BATCH	: 1
		DATE RECEIVED	: 8-APR-2022
		DATE OF ISSUE	: 14-APR-2022
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

#### General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action United Environmental Services & Consulting.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

*Signatories*

*Position*

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

**ALS Technichem (HK) Pty Ltd**  
Part of the **ALS Laboratory Group**

11/F. Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong  
Tel. +852 2610 1044 Fax. +852 2610 2021 [www.alsglobal.com](http://www.alsglobal.com)

WORK ORDER : HK2212152  
SUB-BATCH : 1  
CLIENT : ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING  
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2212152-001	S/N: 3Y6505	AIR	08-Apr-2022	S/N: 3Y6505



# Equipment Verification Report (TSP)

## Equipment Calibrated:

Type: Laser Dust monitor  
 Manufacturer: Sibata LD-3B  
 Serial No. 3Y6505  
 Equipment Ref: EQ114

## Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)  
 Location & Location ID: AUES office (calibration room)  
 Equipment Ref: HVS 018 & HVS 019  
 Last Calibration Date: 22 February 2022

## Equipment Verification Results:

Verification Date: 1 & 7 March 2022

Date	Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in ug/m <sup>3</sup> (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
7-Mar-22	2hr01mins	09:17 ~ 11:18	22.5	1010.6	26.4	783	6.5
7-Mar-22	2hr01mins	11:24 ~ 13:25	22.5	1010.6	34.8	1104	9.1
7-Mar-22	2hr01mins	13:30 ~ 15:31	22.5	1010.6	40.3	2134	17.7
1-Mar-22	30mins	10:03 ~ 10:33	22	1016.9	123.1	1599	53.3
1-Mar-22	31mins	10:39 ~ 11:10	22	1016.9	93.9	1397	45.7

(\* Suspended particle was added into calibration room of HVS019 for high concentration test.

Sensitivity Adjustment Scale Setting (Before Calibration) 591 (CPM)


Sensitivity Adjustment Scale Setting (After Calibration) 588 (CPM)

## Linear Regression of Y or X

Slope (K-factor): 2.0543 (ug/m<sup>3</sup>)/CPM

Correlation Coefficient (R) 0.9875

Date of Issue 26 March 2022

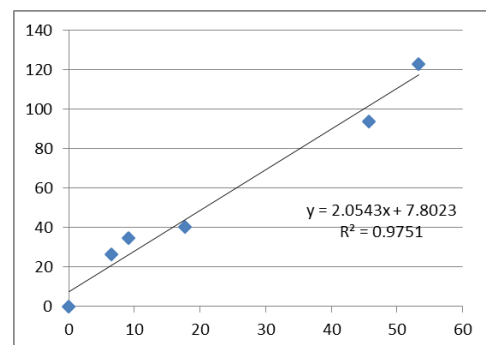

## Remarks:

- Strong** Correlation (R>0.8)
- Factor 2.0543 (ug/m<sup>3</sup>)/CPM should be apply for TSP monitoring

\*If R<0.5, repair or re-verification is required for the equipment

Operator : Fai So Signature : [Signature] Date : 26 March 2022

QC Reviewer : Ben Tam Signature : [Signature] Date : 26 March 2022

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Kwai Chung Date of Calibration: 22-Feb-22  
 Location ID : Calibration Room Next Calibration Date: 22-May-22

### CONDITIONS

Sea Level Pressure (hPa)	1010.8	Corrected Pressure (mm Hg)	758.1
Temperature (°C)	22.8	Temperature (K)	296

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	1.99838
Model->	5025A	Qstd Intercept ->	-0.00903
Calibration Date->	27-Dec-21	Expiry Date->	27-Dec-22

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION		
							Slope =	Intercept =	Corr. coeff. =
18	5.8	5.8	11.6	1.713	54	54.13	27.3242	7.2177	0.9997
13	4.7	4.7	9.4	1.543	49	49.12			
10	3.6	3.6	7.2	1.351	44	44.11			
8	2.3	2.3	4.6	1.080	37	37.09			
5	1.4	1.4	2.8	0.844	30	30.07			

**Calculations :**

$$Qstd = 1/m[\text{sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate  
 IC = corrected chart responses  
 I = actual chart response  
 m = calibrator Qstd slope  
 b = calibrator Qstd intercept  
 Ta = actual temperature during calibration ( deg K )  
 Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\text{sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope  
 b = sampler intercept  
 I = chart response  
 Tav = daily average temperature  
 Pav = daily average pressure

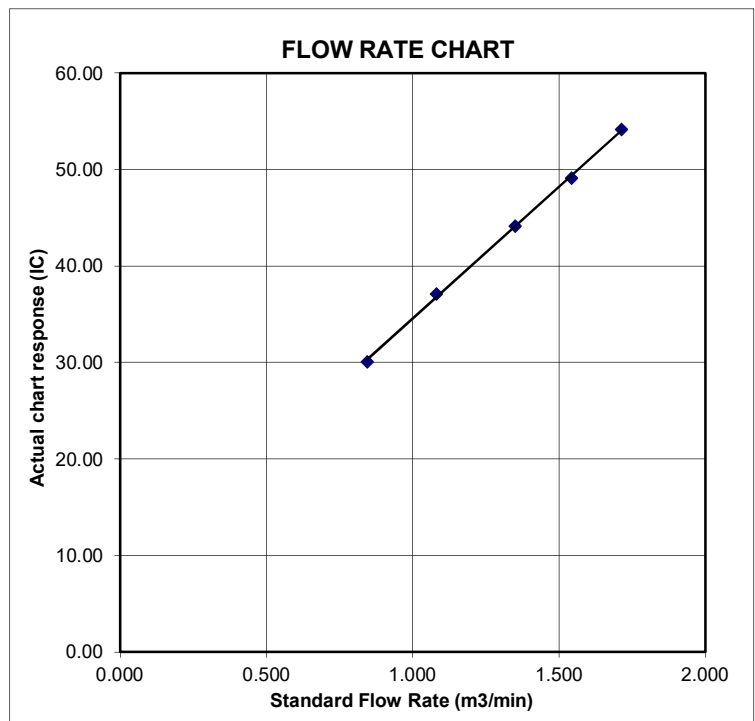

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Kwai Chung Date of Calibration: 22-Feb-22  
 Location ID : Calibration Room Next Calibration Date: 22-May-22

### CONDITIONS

Sea Level Pressure (hPa)	1010.8	Corrected Pressure (mm Hg)	758.1
Temperature (°C)	22.8	Temperature (K)	296

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	1.99838
Model->	5025A	Qstd Intercept ->	-0.00903
Calibration Date->	27-Dec-21	Expiry Date->	27-Dec-22

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.771	52	52.13	Slope = 34.6002 Intercept = -9.1434 Corr. coeff. = 0.9958
13	4.9	4.9	9.8	1.575	44	44.11	
10	3.8	3.8	7.6	1.387	40	40.10	
8	2.4	2.4	4.8	1.104	30	30.07	
5	1.5	1.5	3.0	0.873	20	20.05	

**Calculations :**

$$Q_{std} = 1/m[\sqrt{H_2O(P_a/P_{std})(T_{std}/T_a)}] - b$$


$$IC = I[\sqrt{P_a/P_{std}}(T_{std}/T_a)]$$

Qstd = standard flow rate  
 IC = corrected chart responses  
 I = actual chart response  
 m = calibrator Qstd slope  
 b = calibrator Qstd intercept  
 Ta = actual temperature during calibration ( deg K )  
 Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\sqrt{298/T_{av}}(P_{av}/760)] - b)$$

m = sampler slope  
 b = sampler intercept  
 I = chart response  
 Tav = daily average temperature  
 Pav = daily average pressure

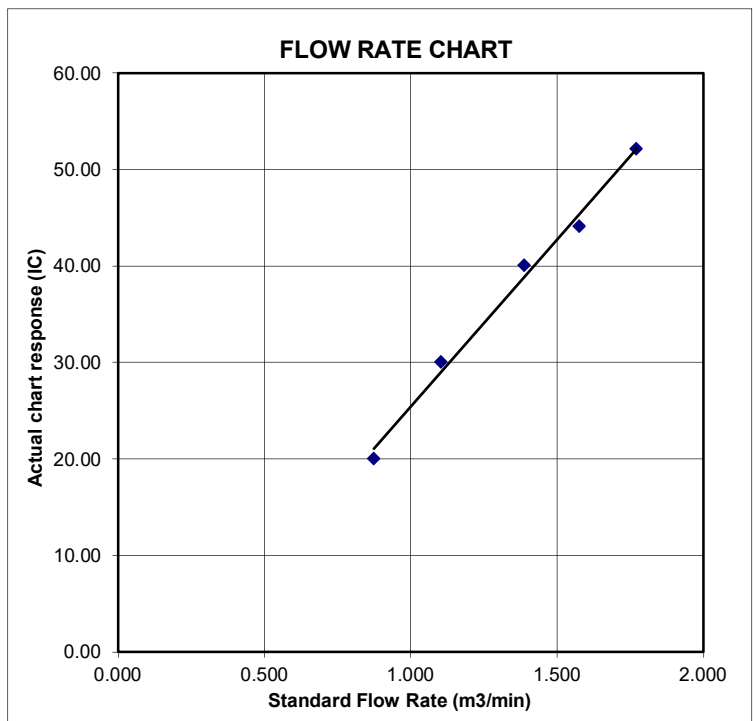



# Certificate of Calibration

Calibration Certification Information			
Cal. Date: December 27, 2021	Rootsmeter S/N: 438320	Ta: 295	°K
Operator: Jim Tisch		Pa: 740.4	mm Hg
Calibration Model #: TE-5025A	Calibrator S/N: <b>1612</b>		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3890	3.2	2.00
2	3	4	1	0.9760	6.4	4.00
3	5	6	1	0.8740	7.9	5.00
4	7	8	1	0.8320	8.8	5.50
5	9	10	1	0.6870	12.7	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left( \frac{Ta}{Pa} \right)}$ (y-axis)
0.9799	0.7055	1.4029	0.9957	0.7168	0.8927
0.9756	0.9996	1.9841	0.9914	1.0157	1.2624
0.9736	1.1140	2.2183	0.9893	1.1320	1.4114
0.9724	1.1688	2.3265	0.9881	1.1876	1.4803
0.9673	1.4079	2.8059	0.9828	1.4306	1.7853
<b>QSTD</b>	m=	<b>1.99838</b>	<b>QA</b>	m=	<b>1.25135</b>
	b=	<b>-0.00903</b>		b=	<b>-0.00574</b>
	r=	<b>0.99999</b>		r=	<b>0.99999</b>

Calculations			
Vstd=	$\Delta Vol \left( \frac{Pa - \Delta P}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)$	Va=	$\Delta Vol \left( \frac{Pa - \Delta P}{Pa} \right)$
Qstd=	Vstd/ΔTime	Qa=	Va/ΔTime
For subsequent flow rate calculations:			
Qstd=	$1/m \left( \left( \sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa=	$1/m \left( \left( \sqrt{\Delta H \left( \frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30



## ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

### SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: <b>HK2212657</b>
CLIENT	: <b>ACTION-UNITED ENVIRONMENTAL SERVICES &amp; CONSULTING</b>		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T.	SUB-BATCH	: 1
		DATE RECEIVED	: 8-APR-2022
		DATE OF ISSUE	: 14-APR-2022
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

#### General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action United Environmental Services & Consulting.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

*Signatories*

*Position*

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

**ALS Technichem (HK) Pty Ltd**  
Part of the **ALS Laboratory Group**

11/F. Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong  
Tel. +852 2610 1044 Fax. +852 2610 2021 [www.alsglobal.com](http://www.alsglobal.com)

WORK ORDER : HK2212657  
SUB-BATCH : 1  
CLIENT : ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING  
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2212657-001	S/N: 456658	AIR	08-Apr-2022	S/N: 456658

# Equipment Verification Report (TSP)

## Equipment Calibrated:

Type: Laser Dust monitor  
 Manufacturer: Sibata LD-3B  
 Serial No. 456658  
 Equipment Ref: EQ115

## Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)  
 Location & Location ID: AUES office (calibration room)  
 Equipment Ref: HVS 018 & HVS 019  
 Last Calibration Date: 22 February 2022

## Equipment Verification Results:

Verification Date: 1 & 7 March 2022

Date	Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in ug/m <sup>3</sup> (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
7-Mar-22	2hr01mins	09:17 ~ 11:18	22.5	1010.6	26.4	1004	8.3
7-Mar-22	2hr01mins	11:24 ~ 13:25	22.5	1010.6	34.8	1674	13.8
7-Mar-22	2hr01mins	13:30 ~ 15:31	22.5	1010.6	40.3	1709	14.2
1-Mar-22	30mins	10:03 ~ 10:33	22	1016.9	123.1	1799	60.0
1-Mar-22	31mins	10:39 ~ 11:10	22	1016.9	93.9	1208	39.5

(\* Suspended particle was added into calibration room of HVS019 for high concentration test.

Sensitivity Adjustment Scale Setting (Before Calibration) 702 (CPM)


Sensitivity Adjustment Scale Setting (After Calibration) 711 (CPM)

## Linear Regression of Y or X

Slope (K-factor): 2.0261 (µg/m<sup>3</sup>)/CPM

Correlation Coefficient (R) 0.9927

Date of Issue 26 March 2022

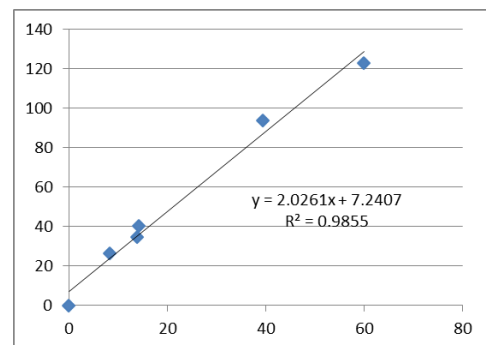

## Remarks:

- Strong** Correlation (R>0.8)
- Factor 2.0261 (µg/m<sup>3</sup>)/CPM should be apply for TSP monitoring

\*If R<0.5, repair or re-verification is required for the equipment

Operator : Fai So Signature : [Signature] Date : 26 March 2022

QC Reviewer : Ben Tam Signature : [Signature] Date : 26 March 2022

## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Kwai Chung Date of Calibration: 22-Feb-22  
 Location ID : Calibration Room Next Calibration Date: 22-May-22

### CONDITIONS

Sea Level Pressure (hPa)	1010.8	Corrected Pressure (mm Hg)	758.1
Temperature (°C)	22.8	Temperature (K)	296

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	1.99838
Model->	5025A	Qstd Intercept ->	-0.00903
Calibration Date->	27-Dec-21	Expiry Date->	27-Dec-22

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.8	5.8	11.6	1.713	54	54.13	Slope = 27.3242 Intercept = 7.2177 Corr. coeff. = 0.9997
13	4.7	4.7	9.4	1.543	49	49.12	
10	3.6	3.6	7.2	1.351	44	44.11	
8	2.3	2.3	4.6	1.080	37	37.09	
5	1.4	1.4	2.8	0.844	30	30.07	

**Calculations :**

$$Qstd = 1/m[\text{sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate  
 IC = corrected chart responses  
 I = actual chart response  
 m = calibrator Qstd slope  
 b = calibrator Qstd intercept  
 Ta = actual temperature during calibration ( deg K )  
 Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\text{sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope  
 b = sampler intercept  
 I = chart response  
 Tav = daily average temperature  
 Pav = daily average pressure

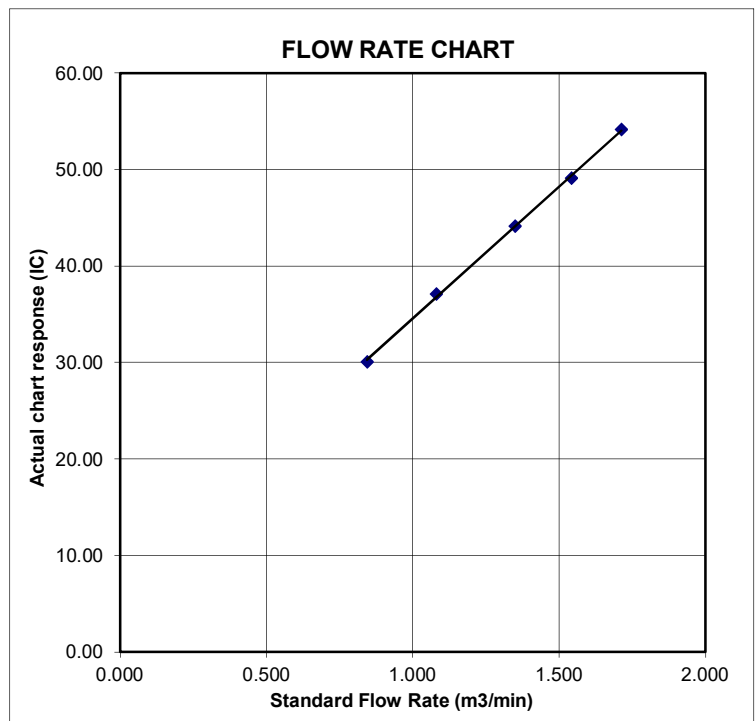



## TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Kwai Chung Date of Calibration: 22-Feb-22  
 Location ID : Calibration Room Next Calibration Date: 22-May-22

### CONDITIONS

Sea Level Pressure (hPa)	1010.8	Corrected Pressure (mm Hg)	758.1
Temperature (°C)	22.8	Temperature (K)	296

### CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	1.99838
Model->	5025A	Qstd Intercept ->	-0.00903
Calibration Date->	27-Dec-21	Expiry Date->	27-Dec-22

### CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.771	52	52.13	Slope = 34.6002 Intercept = -9.1434 Corr. coeff. = 0.9958
13	4.9	4.9	9.8	1.575	44	44.11	
10	3.8	3.8	7.6	1.387	40	40.10	
8	2.4	2.4	4.8	1.104	30	30.07	
5	1.5	1.5	3.0	0.873	20	20.05	

**Calculations :**

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate  
 IC = corrected chart responses  
 I = actual chart response  
 m = calibrator Qstd slope  
 b = calibrator Qstd intercept  
 Ta = actual temperature during calibration ( deg K )  
 Pstd = actual pressure during calibration ( mm Hg )

**For subsequent calculation of sampler flow:**

$$1/m(( I )[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope  
 b = sampler intercept  
 I = chart response  
 Tav = daily average temperature  
 Pav = daily average pressure

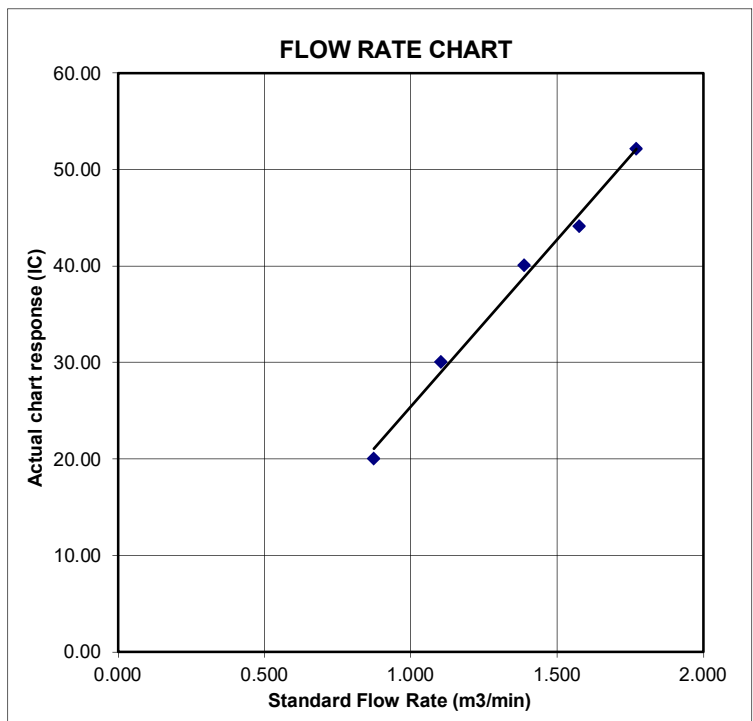



# Certificate of Calibration

Calibration Certification Information			
Cal. Date: December 27, 2021	Rootsmeter S/N: 438320	Ta: 295	°K
Operator: Jim Tisch		Pa: 740.4	mm Hg
Calibration Model #: TE-5025A	Calibrator S/N: <b>1612</b>		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3890	3.2	2.00
2	3	4	1	0.9760	6.4	4.00
3	5	6	1	0.8740	7.9	5.00
4	7	8	1	0.8320	8.8	5.50
5	9	10	1	0.6870	12.7	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left( \frac{Ta}{Pa} \right)}$ (y-axis)
0.9799	0.7055	1.4029	0.9957	0.7168	0.8927
0.9756	0.9996	1.9841	0.9914	1.0157	1.2624
0.9736	1.1140	2.2183	0.9893	1.1320	1.4114
0.9724	1.1688	2.3265	0.9881	1.1876	1.4803
0.9673	1.4079	2.8059	0.9828	1.4306	1.7853
<b>QSTD</b>	m=	<b>1.99838</b>	<b>QA</b>	m=	<b>1.25135</b>
	b=	<b>-0.00903</b>		b=	<b>-0.00574</b>
	r=	<b>0.99999</b>		r=	<b>0.99999</b>

Calculations			
Vstd=	$\Delta Vol \left( \frac{Pa - \Delta P}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)$	Va=	$\Delta Vol \left( \frac{Pa - \Delta P}{Pa} \right)$
Qstd=	Vstd/ΔTime	Qa=	Va/ΔTime
For subsequent flow rate calculations:			
Qstd=	$1/m \left( \left( \sqrt{\Delta H \left( \frac{Pa}{Pstd} \right) \left( \frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa=	$1/m \left( \left( \sqrt{\Delta H \left( \frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30



# Certificate of Calibration 校正證書

Certificate No. : C221365  
證書編號

ITEM TESTED / 送檢項目 ( Job No. / 序引編號 : IC22-0258 )      Date of Receipt / 收件日期 : 14 February 2022

Description / 儀器名稱 : Sound Level Meter (EQ018)  
Manufacturer / 製造商 : Rion  
Model No. / 型號 : NL-52  
Serial No. / 編號 : 00809405  
Supplied By / 委託者 : Action-United Environmental Services and Consulting  
Unit A, 20/F., Gold King Industrial Building,  
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

## TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C      Relative Humidity / 相對濕度 : (50 ± 25)%  
Line Voltage / 電壓 : ---

## TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 12 March 2022

## TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
The results do not exceed manufacturer's specification.  
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Fluke Everett Service Center, USA
- Agilent Technologies / Keysight Technologies

Tested By :   
測試 : K.C. Lee  
Engineer

Certified By :   
核證 : H.C. Chan  
Engineer

Date of Issue : 16 March 2022  
簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C221365

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C220381
CL281	Multifunction Acoustic Calibrator	AV210017

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	94.0	± 1.1

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.0

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

- 6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	94.0	Ref.
			Slow			94.0	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C221365

證書編號

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L <sub>A</sub>	A	Fast	94.00	63 Hz	67.8	-26.2 ± 1.5
					125 Hz	77.9	-16.1 ± 1.5
					250 Hz	85.4	-8.6 ± 1.4
					500 Hz	90.8	-3.2 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	95.0	+1.2 ± 1.6
					4 kHz	94.7	+1.0 ± 1.6
					8 kHz	92.9	-1.1 (+2.1 ; -3.1)
					16 kHz	85.5	-6.6 (+3.5 ; -17.0)

#### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L <sub>C</sub>	C	Fast	94.00	63 Hz	93.2	-0.8 ± 1.5
					125 Hz	93.9	-0.2 ± 1.5
					250 Hz	94.0	0.0 ± 1.4
					500 Hz	94.1	0.0 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	93.6	-0.2 ± 1.6
					4 kHz	92.9	-0.8 ± 1.6
					8 kHz	91.0	-3.0 (+2.1 ; -3.1)
					16 kHz	83.5	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C221365

證書編號

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 16463

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB	: 63 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	16 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

# Certificate of Calibration

## 校正證書

Certificate No. : C221363

證書編號

ITEM TESTED / 送檢項目 ( Job No. / 序引編號 : IC22-0258 )      Date of Receipt / 收件日期 : 14 February 2022

Description / 儀器名稱 : Sound Level Meter (EQ067)  
Manufacturer / 製造商 : Rion  
Model No. / 型號 : NL-31  
Serial No. / 編號 : 00410221  
Supplied By / 委託者 : Action-United Environmental Services and Consulting  
Unit A, 20/F., Gold King Industrial Building,  
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

### TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C      Relative Humidity / 相對濕度 : (50 ± 25)%  
Line Voltage / 電壓 : ---

### TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 12 March 2022

### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
The results do not exceed manufacturer's specification.  
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Fluke Everett Service Center, USA
- Agilent Technologies / Keysight Technologies

Tested By :   
測試 : K C Lee  
Engineer

Certified By :   
核證 : H C Chan  
Engineer

Date of Issue : 16 March 2022  
簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

# Certificate of Calibration

## 校正證書

Certificate No. : C221363  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C220381
CL281	Multifunction Acoustic Calibrator	AV210017

- Test procedure : MA101N.

- Results :

### 6.1 Sound Pressure Level

#### 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.8	± 1.1

#### 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.8 (Ref.)
				104.00		103.8
				114.00		113.7

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

### 6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L <sub>A</sub>	A	Fast	94.00	1	93.8	Ref.
			Slow			93.7	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。



# Certificate of Calibration

## 校正證書

Certificate No. : C221363  
證書編號

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L <sub>A</sub>	A	Fast	94.00	63 Hz	67.5	-26.2 ± 1.5
					125 Hz	77.6	-16.1 ± 1.5
					250 Hz	85.1	-8.6 ± 1.4
					500 Hz	90.5	-3.2 ± 1.4
					1 kHz	93.8	Ref.
					2 kHz	95.0	+1.2 ± 1.6
					4 kHz	94.9	+1.0 ± 1.6
					8 kHz	92.7	-1.1 (+2.1 ; -3.1)
					16 kHz	87.4	-6.6 (+3.5 ; -17.0)

#### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L <sub>C</sub>	C	Fast	94.00	63 Hz	92.8	-0.8 ± 1.5
					125 Hz	93.5	-0.2 ± 1.5
					250 Hz	93.7	0.0 ± 1.4
					500 Hz	93.8	0.0 ± 1.4
					1 kHz	93.7	Ref.
					2 kHz	93.6	-0.2 ± 1.6
					4 kHz	93.1	-0.8 ± 1.6
					8 kHz	90.8	-3.0 (+2.1 ; -3.1)
					16 kHz	85.4	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。



# Certificate of Calibration

## 校正證書

Certificate No. : C221363  
證書編號

Remarks : - UUT Microphone Model No. : UC-53A & S/N : 322551

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz :  $\pm 0.35$  dB  
250 Hz - 500 Hz :  $\pm 0.30$  dB  
1 kHz :  $\pm 0.20$  dB  
2 kHz - 4 kHz :  $\pm 0.35$  dB  
8 kHz :  $\pm 0.45$  dB  
16 kHz :  $\pm 0.70$  dB  
104 dB : 1 kHz :  $\pm 0.10$  dB (Ref. 94 dB)  
114 dB : 1 kHz :  $\pm 0.10$  dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



# Certificate of Calibration

## 校正證書

Certificate No. : C224779  
證書編號

**ITEM TESTED / 送檢項目** ( Job No. / 序引編號 : IC22-1539 )      **Date of Receipt / 收件日期** : 4 August 2022  
**Description / 儀器名稱** : Sound Level Calibrator (EQ085)  
**Manufacturer / 製造商** : Rion  
**Model No. / 型號** : NC-73  
**Serial No. / 編號** : 10655561  
**Supplied By / 委託者** : Action-United Environmental Services and Consulting  
Unit A, 20/F., Gold King Industrial Building,  
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

### TEST CONDITIONS / 測試條件

**Temperature / 溫度** : (23 ± 2)°C      **Relative Humidity / 相對濕度** : (50 ± 25)%  
**Line Voltage / 電壓** : ---

### TEST SPECIFICATIONS / 測試規範

Calibration check

**DATE OF TEST / 測試日期** : 20 August 2022

### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
The results do not exceed manufacturer's specification & user's specified acceptance criteria.  
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

**Tested By / 測試** :   
H T Wong  
Assistant Engineer

**Certified By / 核證** :   
K C Lee  
Engineer

**Date of Issue / 簽發日期** : 23 August 2022

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.  
本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C224779

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
2. The results presented are the mean of 3 measurements at each calibration point.
3. Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C223647
CL281	Multifunction Acoustic Calibrator	AV210017
TST150A	Measuring Amplifier	C221750

4. Test procedure : MA100N.

5. Results :

### 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.5	± 0.2

### 5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	User's Spec.	Uncertainty of Measured Value (Hz)
1	0.953	1 kHz ± 6 %	± 1

Remarks : - The user's specified acceptance criteria (user's spec.) is a customer pre-defined operating tolerance of the UUT, suitable for one's own intended use.

- The uncertainties are for a confidence probability of not less than 95 %.

### Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。



## REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

**CONTACT:** MR BEN TAM  
**CLIENT:** ACTION-UNITED ENVIRONMENTAL SERVICES &  
CONSULTING  
**ADDRESS:** RM A 20/F., GOLD KING IND BLDG,  
NO. 35-41 TAI LIN PAI ROAD,  
KWAI CHUNG, N.T.

**WORK ORDER:** HK2251569  
**SUB-BATCH:** 0  
**LABORATORY:** HONG KONG  
**DATE RECEIVED:** 29-Dec-2022  
**DATE OF ISSUE:** 05-Jan-2023

### SPECIFIC COMMENTS

Equipment information (Brand name, Model No., Serial No. and Equipment No.) is provided by client. The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principle as practised by the laboratory or quoted from relevant international standards.

The validity of equipment/ meter performance only applies to the result(s) stated in the report.

Equipment Type: Multifunctional Meter

Service Nature: Performance Check

Scope: Conductivity, Dissolved Oxygen, pH Value, Turbidity, Salinity and Temperature

Brand Name/ Model No.: [YSI]/ [Professional DSS]

Serial No./ Equipment No.: [17B102764/17B100758]/ [EQW019]

Date of Calibration: 04-January-2023

### GENERAL COMMENTS

This report superseded any previous report(s) with same work order number.

Ms. Lin Wai Yu, Iris  
Assistant Manager - Inorganics

# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



**WORK ORDER:** HK2251569  
**SUB-BATCH:** 0  
**DATE OF ISSUE:** 05-Jan-2023  
**CLIENT:** ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING

Equipment Type: Multifunctional Meter  
Brand Name/ Model No.: [YSI]/ [Professional DSS]  
Serial No./ Equipment No.: [17B102764/17B100758]/ [EQW019]  
Date of Calibration: 04-January-2023 Date of Next Calibration: 04-April-2023

## PARAMETERS:

### Conductivity

Method Ref: APHA (23rd edition), 2510B

Expected Reading ( $\mu\text{S}/\text{cm}$ )	Displayed Reading ( $\mu\text{S}/\text{cm}$ )	Tolerance (%)
146.9	156.1	+6.3
6667	7092	+6.4
12890	13808	+7.1
58670	61025	+4.0
	Tolerance Limit (%)	$\pm 10.0$

### Dissolved Oxygen

Method Ref: APHA (23rd edition), 4500O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.03	3.14	+0.11
4.68	4.77	+0.09
7.37	7.37	+0.00
	Tolerance Limit (mg/L)	$\pm 0.20$

### pH Value

Method Ref: APHA (23rd edition), 4500H: B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)
4.0	3.80	-0.20
7.0	7.05	+0.05
10.0	9.96	-0.04
	Tolerance Limit (pH unit)	$\pm 0.20$

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu, Iris  
Assistant Manager - Inorganics

# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



**WORK ORDER:** HK2251569  
**SUB-BATCH:** 0  
**DATE OF ISSUE:** 05-Jan-2023  
**CLIENT:** ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING

Equipment Type: Multifunctional Meter  
Brand Name/ Model No.: [YSI]/ [Professional DSS]  
Serial No./ Equipment No.: [17B102764/17B100758]/ [EQW019]  
Date of Calibration: 04-January-2023 Date of Next Calibration: 04-April-2023

## PARAMETERS:

### Turbidity

Method Ref: APHA (23rd edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	-0.92	--
4	4.37	+9.3
40	37.54	-6.2
80	73.45	-8.2
400	370.84	-7.3
800	725.48	-9.3
	Tolerance Limit (%)	±10.0

### Salinity

Method Ref: APHA (23rd edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	--
10	10.61	+6.1
20	21.35	+6.8
30	31.14	+3.8
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu, Iris  
Assistant Manager - Inorganics

# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



**WORK ORDER:** HK2251569  
**SUB-BATCH:** 0  
**DATE OF ISSUE:** 05-Jan-2023  
**CLIENT:** ACTION-UNITED ENVIRONMENTAL SERVICES & CONSULTING

Equipment Type: Multifunctional Meter  
Brand Name/ Model No.: [YSI]/ [Professional DSS]  
Serial No./ Equipment No.: [17B102764/17B100758]/ [EQW019]  
Date of Calibration: 04-January-2023 Date of Next Calibration: 04-April-2023

## PARAMETERS:

### Temperature

**Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.**

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
7.5	8.5	+1.0
20.5	21.0	+0.5
42.0	42.0	+0.0
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Ms. Lin Wai Yu, Iris  
Assistant Manager - Inorganics



# WATER

## Manufacturing Certificate

This product has been tested in accordance with procedures established through Global Water Instrumentation's Quality Management System. This product meets or exceeds its manufacturing acceptance criteria.

<b>ITEM DESCRIPTION:</b>	Flow Probe, 5.5 - 14'
<b>MODEL NAME/ NUMBER:</b>	FP211
<b>PART NUMBER:</b>	BB1100
<b>SERIAL NUMBER:</b>	22B106785
<b>ACCURACY:</b>	± 0.1 FPS (0.03 MPS)
<b>POWER REQUIRED:</b>	Internal Lithium Coin Cell Battery
<b>CABLE LENGTH:</b>	N/A
<b>CERTIFICATES:</b>	CE Compliant
<b>RANGE:</b>	0.3 - 19.9 FPS (0.1 - 6.1 MPS)
<b>OUTPUT:</b>	Flow Display, FPS/MPS
<b>CALIBRATION FACTOR:</b>	318

Contact  
Global Water  
for all your  
instrumentation  
needs:

Water Level

Water Flow

Water Samplers

Water Quality

Weather

Remote Monitoring

Control

Technician *Barnette, Melinda*

Inspector *Winberg, Josh*

Date *3/5/2022*

**NOTE:** Global Water Instrumentation warrants that its products are free from defects in material & workmanship under normal use & service for a period of one year from date of original shipment from factory. Repaired components are warranted for a period of 90 days from shipment. Contact us for complete warranty details.



**Global Water**  
a xylem brand

In the U.S. call toll free  
at 1-800-876-1172  
International: 1-979-690-5560  
Fax: 1-979-690-0440  
Email: [globalw@globalw.com](mailto:globalw@globalw.com)

Visit our online catalog at:  
[www.globalw.com](http://www.globalw.com)  
Our Service Address:  
151 Graham Rd  
College Station, TX 77845





Hong Kong Accreditation Service  
香港認可處

**Certificate of Accreditation**  
**認可證書**

*This is to certify that*  
特此證明

**ALS TECHNICHEM (HK) PTY LIMITED**

**11/F, Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong**  
香港新界葵涌永業街1-3號忠信針織中心11樓

*is accredited by the Hong Kong Accreditation Service (HKAS) to ISO/IEC 17025:2017  
for performing specific laboratory activities as listed in the scope of accreditation within the test category of*  
獲香港認可處根據ISO/IEC 17025:2017認可  
進行載於認可範圍內下述測試類別中的指定實驗所活動

**Environmental Testing**  
**環境測試**

*This accreditation to ISO/IEC 17025:2017 demonstrates technical competence for a defined scope and  
the implementation of a management system relevant to laboratory operation  
(see joint IAF-ILAC-ISO Communiqué).*  
此項 ISO/IEC 17025:2017 的認可資格證明此實驗所具備指定範疇內所須的技術能力並  
實施一套與實驗所運作相關的管理體系  
(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

*The common seal of HKAS is affixed hereto by the authority of the HKAS Executive*  
現經香港認可處執行機關授權在此蓋上香港認可處的印章

  
SHUM Wai-leung, Executive Administrator  
執行幹事 沈偉良  
Issue Date : 28 February 2020  
簽發日期：二零二零年二月二十八日

Registration Number : HOKLAS 066  
註冊號碼：



Date of First Registration : 15 September 1995  
首次註冊日期：一九九五年九月十五日

## **Appendix F**

### **Event and Action Plan of Air Quality, Noise and Water Quality**

### Event and Action Plan for air quality

Event	Action			
	ET	IEC	ER	Contractor
Action level exceedance for one sample	<ol style="list-style-type: none"> <li>1. Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>2. Inform IEC and ER;</li> <li>3. Repeat measurement to confirm finding;</li> <li>4. Increase monitoring frequency to daily.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify Contractor</li> </ol>	<ol style="list-style-type: none"> <li>1. Rectify any unacceptable practice;</li> <li>2. Amend working methods if appropriate.</li> </ol>
Action level exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>1. Identify source;</li> <li>2. Inform IEC and ER;</li> <li>3. Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>4. Repeat measurements to confirm findings;</li> <li>5. Increase monitoring frequency to daily;</li> <li>6. Discuss with IEC and Contractor on remedial actions required;</li> <li>7. If exceedance continues, arrange meeting with IEC and ER;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss with ET and Contractor on possible remedial measures;</li> <li>4. Advise the ET on the effectiveness of the proposed remedial measures;</li> <li>5. Supervise Implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Ensure remedial measures properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit proposals for remedial to ER within 3 working days of notification;</li> <li>2. Implement the agreed proposals;</li> <li>3. Amend proposal if appropriate.</li> </ol>
Limit level exceedance for one sample	<ol style="list-style-type: none"> <li>1. Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>2. Inform ER, Contractor and EPD;</li> <li>3. Repeat measurement to confirm finding;</li> <li>4. Increase monitoring frequency to daily;</li> <li>5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contractor's working method;</li> <li>3. Discuss with ET and Contractor on possible remedial measures;</li> <li>4. Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>5. Supervise implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Ensure remedial measures properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Amend proposal if appropriate.</li> </ol>
Limit level exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>1. Notify IEC, ER, Contractor and EPD;</li> <li>2. Identify source;</li> <li>3. Repeat measurement to confirm findings;</li> <li>4. Increase monitoring frequency to daily;</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Ensure remedial measures properly implemented;</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Resubmit proposals if problem still not under control;</li> <li>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>

Note: ET – Environmental Team IEC – Independent Environmental Checker ER – Engineer's Representative

### Event and Action Plan for Construction Noise

Event	Action			
	ET	IEC	ER	Contractor
Action Level Exceedance	<ol style="list-style-type: none"> <li>1. Notify IEC, ER and Contractor;</li> <li>2. Carry out investigation;</li> <li>3. Report the results of investigation to the IEC, ER and Contractor;</li> <li>4. Discuss with the Contractor and formulate remedial measures;</li> <li>5. Increase monitoring frequency to check mitigation effectiveness</li> </ol>	<ol style="list-style-type: none"> <li>1. Review the analyzed results submitted by the ET;</li> <li>2. Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analyzed noise problem;</li> <li>4. Ensure remedial measures are properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit noise mitigation proposals to IEC and ER;</li> <li>2. Implement noise mitigation proposals</li> </ol>
Limit Level Exceedance	<ol style="list-style-type: none"> <li>1. Identify source;</li> <li>2. Inform IEC, ER, EPD and Contractor;</li> <li>3. Repeat measurements to confirm findings;</li> <li>4. Increase monitoring frequency;</li> <li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>6. Inform IEC, ER and EPD the causes and actions taken for the exceedances;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>3. Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. Require Contractor to propose remedial measures for the analyzed noise problem;</li> <li>4. Ensure remedial measures properly implemented;</li> <li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Resubmit proposals if problem still not under control;</li> <li>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>

Note:

ET – Environmental Team

IEC – Independent Environmental Checker

ER – Engineer's Representative

### Event and Action Plan for Water Quality

Event	Action			
	ET	IEC	ER	Contractor
Action level exceedance for one sampling day	<ol style="list-style-type: none"> <li>1. Inform IEC, Contractor and ER;</li> <li>2. Check monitoring data, all plant, equipment and Contractor's working methods; and</li> <li>3. Discuss remedial measures with IEC and Contractor and ER.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET, ER and Contractor on the implemented mitigation measures;</li> <li>2. Review proposals on remedial measures submitted by Contractor and advise the ER accordingly; and</li> <li>3. Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with IEC, ET and Contractor on the implemented mitigation measures;</li> <li>2. Make agreement on the remedial measures to be implemented;</li> <li>3. Supervise the implementation of agreed remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Identify source(s) of impact;</li> <li>2. Inform the ER and confirm notification of the non-compliance in writing;</li> <li>3. Rectify unacceptable practice;</li> <li>4. Check all plant and equipment;</li> <li>5. Consider changes of working methods;</li> <li>6. Discuss with ER, ET and IEC and purpose remedial measures to IEC and ER; and</li> <li>7. Implement the agreed mitigation measures.</li> </ol>
Action level exceedance for more than one consecutive sampling days	<ol style="list-style-type: none"> <li>1. Repeat in-situ measurement on next day of exceedance to confirm findings;</li> <li>2. Inform IEC, contractor and ER;</li> <li>3. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>4. Discuss remedial measures with IEC, contractor and ER</li> <li>5. Ensure remedial measures are implemented</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET, Contractor and ER on the implemented mitigation measures;</li> <li>2. Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and</li> <li>3. Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET, IEC and Contractor on the proposed mitigation measures;</li> <li>2. Make agreement on the remedial measures to be implemented ; and</li> <li>3. Discuss with ET, IEC and Contractor on the effectiveness of the implemented remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Identify source(s) of impact;</li> <li>2. Inform the ER and confirm notification of the non-compliance in writing;</li> <li>3. Rectify unacceptable practice;</li> <li>4. Check all plant and equipment and consider changes of working methods;</li> <li>5. Discuss with ET, IEC and ER and submit proposal of remedial measures to ER and IEC within 3 working days of notification; and</li> <li>6. Implement the agreed mitigation measures.</li> </ol>
Limit level exceedance for one sampling day	<ol style="list-style-type: none"> <li>1. Repeat measurement on next day of exceedance to confirm findings;</li> <li>2. Inform IEC, contractor and ER;</li> <li>3. Rectify unacceptable practice;</li> <li>4. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>6. Consider changes of working methods;</li> <li>7. Discuss mitigation measures with IEC, ER and Contractor; and</li> <li>8. Ensure the agreed remedial measures are implemented</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET, Contractor and ER on the implemented mitigation measures;</li> <li>2. Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and</li> <li>3. Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET, IEC and Contractor on the implemented remedial measures;</li> <li>2. Request Contractor to critically review the working methods;</li> <li>3. Make agreement on the remedial measures to be implemented; and</li> <li>4. Discuss with ET, IEC and Contractor on the effectiveness of the implemented remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Identify source(s) of impact;</li> <li>2. Inform the ER and confirm notification of the non-compliance in writing;</li> <li>3. Rectify unacceptable practice;</li> <li>4. Check all plant and equipment and consider changes of working methods;</li> <li>5. Discuss with ET, IEC and ER and submit proposal of additional mitigation measures to ER and IEC within 3 working days of notification; and</li> <li>6. Implement the agreed remedial measures.</li> </ol>
Limit level exceedance for more than one consecutive sampling days	<ol style="list-style-type: none"> <li>1. Inform IEC, contractor and ER;</li> <li>2. Check monitoring data, all plant, equipment and Contractor's working methods;</li> <li>3. Discuss mitigation measures with IEC, ER and Contractor;</li> <li>4. Ensure mitigation measures are implemented; and</li> <li>5. Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET, Contractor and ER on the implemented mitigation measures;</li> <li>2. Review the proposed remedial measures submitted by Contractor and advise the ER accordingly; and</li> <li>3. Review and advise the ET and ER on the effectiveness of the implemented mitigation measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss with ET, IEC and Contractor on the implemented remedial measures;</li> <li>2. Request Contractor to critically review the working methods;</li> <li>3. Make agreement on the remedial measures to be implemented;</li> <li>4. Discuss with ET and IEC on the effectiveness of the implemented mitigation measures; and</li> <li>5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level.</li> </ol>	<ol style="list-style-type: none"> <li>1. Identify source(s) of impact;</li> <li>2. Inform the ER and confirm notification of the non-compliance in writing;</li> <li>3. Rectify unacceptable practice;</li> <li>4. Check all plant and equipment and consider changes of working methods;</li> <li>5. Discuss with ET, IEC and ER and submit proposal of additional mitigation measures to ER and IEC within 3 working days of notification; and</li> <li>6. Implement the agreed remedial measures; and</li> <li>7. As directed by the ER, to slow down or stop all or part of the construction activities until no exceedance of Limit level.</li> </ol>

Note: ET – Environmental Team IEC – Independent Environmental Checker ER – Engineer's Representative  
 Each step of actions required shall be implemented within 1 working day unless otherwise specified or agreed with EPD.

## **Appendix G**

### **Monitoring Schedules of the Reporting Month and Coming Month**

**Impact Monitoring Schedule of Air Quality, Noise and Water Quality – February 2023**

Date		Noise Monitoring	Air Quality Monitoring		Water Quality
			1-Hour TSP	24-Hour TSP	
Wed	1-Feb-23				✓
Thu	2-Feb-23			✓	
Fri	3-Feb-23				✓
Sat	4-Feb-23				
Sun	5-Feb-23				
Mon	6-Feb-23	✓	✓		✓
Tue	7-Feb-23				
Wed	8-Feb-23			✓	✓
Thu	9-Feb-23				
Fri	10-Feb-23				✓
Sat	11-Feb-23		✓		
Sun	12-Feb-23				
Mon	13-Feb-23				✓
Tue	14-Feb-23			✓	
Wed	15-Feb-23				✓
Thu	16-Feb-23				
Fri	17-Feb-23	✓	✓		✓
Sat	18-Feb-23				
Sun	19-Feb-23				
Mon	20-Feb-23			✓	✓
Tue	21-Feb-23				
Wed	22-Feb-23				✓
Thu	23-Feb-23	✓	✓		
Fri	24-Feb-23				✓
Sat	25-Feb-23			✓	
Sun	26-Feb-23				
Mon	27-Feb-23				✓
Tue	28-Feb-23				

✓	Monitoring Day
	Sunday or Public Holiday



**Impact Monitoring Schedule of Air Quality, Noise and Water Quality – March 2023**

Date		Noise Monitoring	Air Quality Monitoring		Water Quality
			1-Hour TSP	24-Hour TSP	
Wed	1-Mar-23	✓	✓		✓
Thu	2-Mar-23				
Fri	3-Mar-23			✓	✓
Sat	4-Mar-23				
Sun	5-Mar-23				
Mon	6-Mar-23				✓
Tue	7-Mar-23	✓	✓		
Wed	8-Mar-23				✓
Thu	9-Mar-23			✓	
Fri	10-Mar-23				✓
Sat	11-Mar-23				
Sun	12-Mar-23				
Mon	13-Mar-23	✓	✓		✓
Tue	14-Mar-23				
Wed	15-Mar-23			✓	✓
Thu	16-Mar-23				
Fri	17-Mar-23				✓
Sat	18-Mar-23		✓		
Sun	19-Mar-23				
Mon	20-Mar-23				✓
Tue	21-Mar-23			✓	
Wed	22-Mar-23				✓
Thu	23-Mar-23				
Fri	24-Mar-23	✓	✓		✓
Sat	25-Mar-23				
Sun	26-Mar-23				
Mon	27-Mar-23			✓	✓
Tue	28-Mar-23				
Wed	29-Mar-23				✓
Thu	30-Mar-23	✓	✓		
Fri	31-Mar-23				✓

✓	Monitoring Day
	Sunday or Public Holiday

## **Appendix H**

### **Monitoring Data**

- **24-hour TSP Air Quality**
- **Noise**
- **Water Quality**

## **Air Quality (24-hour TSP)**

**24-Hour TSP Monitoring Data for ASR-1**

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (°C)	AVG AIR PRESS (hPa)	STANDARD FLOW RATE (m <sup>3</sup> /min)	AIR VOLUME (std m <sup>3</sup> )	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED (g)	24-Hr TSP (µg/m <sup>3</sup> )
		INITIAL	FINAL	(min)	MIN	MAX	AVG					INITIAL	FINAL		
2 Feb 23	28980	26638.71	26662.71	1440.00	39	39	39.0	19.4	1018.2	1.20	1733	2.8351	2.9446	0.1095	63
8 Feb 23	29107	26662.71	26686.71	1440.00	39	39	39.0	18.5	1017.1	1.21	1746	2.7278	2.7873	0.0595	34
14 Feb 23	29110	26686.71	26710.71	1440.00	39	39	39.0	18.5	1018.8	1.21	1748	2.7224	2.7913	0.0689	39
20 Feb 23	29131	26710.71	26734.71	1440.00	39	39	39.0	20.1	1019.2	1.21	1743	2.7409	2.7951	0.0542	31
25 Feb 23	29146	26734.71	26758.71	1440.00	39	39	39.0	17.1	1026.5	1.26	1809	2.7389	2.8690	0.1301	72

**24-Hour TSP Monitoring Data for ASR-2**

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (°C)	AVG AIR PRESS (hPa)	STANDARD FLOW RATE (m <sup>3</sup> /min)	AIR VOLUME (std m <sup>3</sup> )	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED (g)	24-Hr TSP (µg/m <sup>3</sup> )
		INITIAL	FINAL	(min)	MIN	MAX	AVG					INITIAL	FINAL		
2 Feb 23	28988	24077.36	24101.36	1440.00	42	42	42.0	19.4	1018.2	1.31	1888	2.8323	3.0756	0.2433	129
8 Feb 23	29105	24101.36	24125.36	1440.00	41	41	41.0	18.5	1017.1	1.29	1857	2.7367	2.8375	0.1008	54
14 Feb 23	29122	24125.36	24149.36	1440.00	41	41	41.0	18.5	1018.8	1.29	1858	2.7338	2.8081	0.0743	40
20 Feb 23	29142	24149.36	24173.36	1440.00	42	42	42.0	20.1	1019.2	1.28	1847	2.7315	2.8079	0.0764	41
25 Feb 23	29144	24173.36	24197.36	1440.00	41	41	41.0	17.1	1026.5	1.26	1821	2.7365	2.9790	0.2425	133

**24-Hour TSP Monitoring Data for ASR-3a**

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (°C)	AVG AIR PRESS (hPa)	STANDARD FLOW RATE (m <sup>3</sup> /min)	AIR VOLUME (std m <sup>3</sup> )	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED (g)	24-Hr TSP (µg/m <sup>3</sup> )
		INITIAL	FINAL	(min)	MIN	MAX	AVG					INITIAL	FINAL		
2 Feb 23	28989	17845.11	17869.11	1440.00	39	39	39	19.4	1018.2	1.24	1784	2.8388	2.9262	0.0874	49
8 Feb 23	29108	17869.11	17893.11	1440.00	40	40	40	18.5	1017.1	1.28	1841	2.7308	2.9458	0.2150	117
14 Feb 23	29109	17893.11	17917.11	1440.00	40	40	40	18.5	1018.8	1.28	1843	2.7244	2.7571	0.0327	18
20 Feb 23	29143	17917.11	17941.11	1440.00	40	40	40	20.1	1019.2	1.28	1850	2.7331	2.8126	0.0795	43
25 Feb 23	29145	17941.11	17965.11	1440.00	39	39	39	17.1	1026.5	1.26	1820	2.7379	2.7771	0.0392	22

## Noise

Noise Measurement Results (dB(A)) of CN-1																					
Date	Start Time	1 <sup>st</sup> Leq <sub>5min</sub>	L10	L90	2 <sup>nd</sup> Leq <sub>5min</sub>	L10	L90	3 <sup>rd</sup> Leq <sub>5min</sub>	L10	L90	4 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	5 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	6 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	Leq <sub>30min</sub>	Façade Correction (*)
6 Feb 23	13:02	58.3	60.9	51	60.6	62.5	54.2	68	72.2	55.7	61.9	63.3	55.8	60.9	63.6	56	58.8	61.7	48.9	63	66
17 Feb 23	14:05	60.2	63	56.5	59.3	63	56	62.6	65	57	63.3	65.5	57.5	65.2	67	58.5	65.6	67	59.5	63	66
23 Feb 23	13:00	60.8	63	55.5	60.7	63	56	62.3	65	58	63.4	66	58	63.2	65.5	56	60.5	63.5	56	62	65

(\*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

Noise Measurement Results (dB(A)) of CN-2																					
Date	Start Time	1 <sup>st</sup> Leq <sub>5min</sub>	L10	L90	2 <sup>nd</sup> Leq <sub>5min</sub>	L10	L90	3 <sup>rd</sup> Leq <sub>5min</sub>	L10	L90	4 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	5 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	6 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	Leq <sub>30min</sub>	Façade Correction (*)
6 Feb 23	13:36	68.6	64.7	52.2	60.9	64.5	53.3	61.7	62.2	55	59.5	61.4	51.7	59.3	60.1	51.3	61.1	64.9	52.4	63	66
17 Feb 23	10:48	53.6	59.5	48.5	56.2	60.5	49	57.5	62	52	57.5	63.5	50.5	58.6	65	52	57.2	63	51	57	60
23 Feb 23	13:35	56.8	63	52	57.2	65	52	57.5	63.5	51	55.8	60	49	56.2	60	48.5	55.5	59.5	48.5	57	60

(\*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

Noise Measurement Results (dB(A)) of CN-3																					
Date	Start Time	1 <sup>st</sup> Leq <sub>5min</sub>	L10	L90	2 <sup>nd</sup> Leq <sub>5min</sub>	L10	L90	3 <sup>rd</sup> Leq <sub>5min</sub>	L10	L90	4 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	5 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	6 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	Leq <sub>30min</sub>	Façade Correction (*)
6 Feb 23	14:10	58.2	62.5	53.1	57.9	59.9	53.4	58.1	59.7	54.1	57.8	59.5	54.2	56.7	59.2	52.9	58.5	60.8	55	58	61
17 Feb 23	9:58	59.6	64.5	55	60.2	65	56	58.6	63	55	59.8	63	55	60.7	63.5	56.5	61.5	64	57	60	63
23 Feb 23	14:09	58.2	63	54	59.7	63	55	59.2	63	55.5	61.8	65	58	60.9	63.5	58	62.2	65	58	61	64

(\*) A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

Noise Measurement Results (dB(A)) of CN-4																					
Date	Start Time	1 <sup>st</sup> Leq <sub>5min</sub>	L10	L90	2 <sup>nd</sup> Leq <sub>5min</sub>	L10	L90	3 <sup>rd</sup> Leq <sub>5min</sub>	L10	L90	4 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	5 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	6 <sup>th</sup> Leq <sub>5min</sub>	L10	L90	Leq <sub>30min</sub>	Façade Correction (*)
6 Feb 23	14:43	68.6	62.7	52.1	60.7	64.4	51.5	58.8	61.7	50.7	58.9	62.7	52.2	58.6	59.3	51.3	57.9	60.7	51.3		63
17 Feb 23	13:10	60.8	65	56.5	59.6	65	56	59.2	63.5	55.5	62.2	65.5	56.5	63	66	57	62.5	65.5	57		61
23 Feb 23	14:48	62.8	64.5	57	63.3	65	57	61.7	64	56.5	59.8	65	56	61.7	65	56.5	58.5	63.5	55.5		62

## **Water Quality**

**Water Quality Impact Monitoring Result for M1**

Date																		
1 Feb 23																		
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	9:30	0.13	16.2	16.2	<0.1	<0.1	8.8	8.80	94.6	94.6	1.23	1.3	7.18	7.2	0.05	0.05	6	6.5
			16.2		<0.1		8.79		94.5		1.28		7.18		0.05		7	

Date																		
3 Feb 23																		
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	11:30	0.12	17.5	17.5	<0.1	<0.1	8.79	8.81	97.3	97.5	1.08	1.1	8.70	8.7	0.05	0.05	<2	<2
			17.5		<0.1		8.82		97.6		1.09		8.70		0.05		<2	

Date																		
6 Feb 23																		
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	9:30	0.14	17.5	17.5	<0.1	<0.1	8.6	8.60	97.3	97.2	1.79	1.8	7.40	7.4	0.05	0.05	<2	<2
			17.5		<0.1		8.59		97.1		1.82		7.40		0.05		<2	

Date																		
8 Feb 23																		
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	9:40	0.13	18.5	18.5	<0.1	<0.1	8.49	8.48	96.0	95.9	1.03	1.0	7.15	7.2	0.05	0.05	<2	<2
			18.5		<0.1		8.47		95.8		1.05		7.15		0.05		<2	

Date																		
10 Feb 23																		
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	9:30	0.14	18.5	18.5	<0.1	<0.1	8.47	8.46	95.7	95.6	1.42	1.4	7.56	7.6	0.05	0.05	<2	<2
			18.5		<0.1		8.44		95.4		1.38		7.56		0.05		<2	

Date																		
13 Feb 23																		
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	9:30	0.13	19.6	19.6	<0.1	<0.1	8.28	8.28	94.9	94.9	1.08	1.1	7.95	8.0	0.05	0.05	<2	<2
			19.6		<0.1		8.27		94.8		1.06		7.95		0.05		<2	



Date		15 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	9:30	0.13	18.9	18.9	<0.1	<0.1	8.34	8.34	94.8	95.3	1.05	1.0	7.58	7.6	0.05	0.05	4	4.5
			18.9		<0.1		8.33		95.7		1.02		7.58		0.05		5	

Date		17 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	9:30	0.14	19.5	19.5	<0.1	<0.1	8.36	8.37	96.1	96.2	1.2	1.2	8.02	8.0	0.05	0.05	<2	<2
			19.5		<0.1		8.37		96.2		1.21		8.02		0.05		<2	

Date		20 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	9:30	0.14	16.9	16.9	<0.1	<0.1	9.19	9.20	97.8	97.9	0.18	0.2	7.93	7.9	0.05	0.05	6	6.5
			16.9		<0.1		9.2		98.0		0.17		7.93		0.05		7	

Date		22 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	9:30	0.14	16.8	16.8	<0.1	<0.1	10.16	10.21	108.5	109.1	2	2.0	8.22	8.2	0.05	0.05	4	5.0
			16.8		<0.1		10.26		109.6		1.99		8.22		0.05		6	

Date		24 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	9:30	0.13	18	18.0	<0.1	<0.1	8.64	8.62	95.1	94.9	3.21	3.2	7.22	7.2	0.05	0.05	<2	<2
			18		<0.1		8.59		94.6		3.19		7.22		0.05		<2	

Date		27 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M1	10:30	0.14	16.1	16.1	<0.1	<0.1	8.41	8.41	82.7	82.8	1.58	1.6	7.74	7.7	0.03	0.03	6	5.5
			16.1		<0.1		8.41		82.8		1.64		7.74		0.03		5	

**Water Quality Impact Monitoring Result for M2**

Date	1 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:00	0.07	16.7	16.7	<0.1	<0.1	8.84	8.84	95.0	94.9	0.48	0.5	7.04	7.0	0.04	0.04	<2	<2
			16.7		<0.1		8.83		94.8		0.5		7.04		0.04		<2	

Date	3 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	11:00	0.07	18.2	18.2	<0.1	<0.1	8.64	8.63	98.6	98.4	0.34	0.4	7.74	7.7	0.05	0.05	<2	<2
			18.2		<0.1		8.61		98.2		0.36		7.74		0.05		<2	

Date	6 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:05	0.07	17.8	17.8	<0.1	<0.1	8.54	8.54	96.9	96.9	3.38	3.4	7.27	7.3	0.08	0.08	<2	<2
			17.8		<0.1		8.54		96.8		3.42		7.27		0.08		<2	

Date	8 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:20	0.08	18.7	18.7	<0.1	<0.1	8.62	8.61	97.5	97.4	2.47	2.5	7.06	7.1	0.04	0.04	2	2.0
			18.7		<0.1		8.6		97.3		2.49		7.06		0.04		2	

Date	10 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:00	0.08	18.9	18.9	<0.1	<0.1	8.61	8.60	97.2	97.0	6.69	6.7	7.28	7.3	0.08	0.08	<2	<2
			18.9		<0.1		8.59		96.8		6.68		7.28		0.08		<2	

Date	13 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:00	0.07	19.8	19.8	<0.1	<0.1	8.23	8.23	94.3	94.3	1.53	1.5	7.85	7.9	0.07	0.07	4	3.5
			19.8		<0.1		8.22		94.2		1.54		7.85		0.07		3	

Date		15 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:15	0.08	18.7	18.7	<0.1	<0.1	8.39	8.39	96.1	96.1	3.52	3.6	7.61	7.6	0.07	0.07	<2	<2
			18.7		<0.1		8.38		96.0		3.6		7.61		0.07		<2	

Date		17 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:10	0.08	19.7	19.7	<0.1	<0.1	8.2	8.20	93.9	93.9	1.15	1.1	8.15	8.2	0.08	0.08	4	4.0
			19.7		<0.1		8.19		93.8		1.1		8.15		0.08		4	

Date		20 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:00	0.07	17.2	17.2	<0.1	<0.1	10.21	10.26	106.4	106.8	1.29	1.3	8.11	8.1	0.07	0.07	7	6.5
			17.2		<0.1		10.3		107.2		1.22		8.10		0.07		6	

Date		22 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:15	0.07	17	17.0	<0.1	<0.1	9.76	9.79	103.9	104.3	1.72	1.7	8.14	8.1	0.07	0.07	3	3.5
			17		<0.1		9.82		104.6		1.68		8.14		0.07		4	

Date		24 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	10:00	0.08	20.6	20.6	<0.1	<0.1	8.93	8.93	99.5	99.5	1.43	1.4	8.05	8.1	0.11	0.11	3	3.5
			20.6		<0.1		8.92		99.4		1.41		8.05		0.11		4	

Date		27 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M2	9:27	0.07	21.5	21.5	<0.1	<0.1	9.02	9.03	102.2	102.3	0.66	0.7	8.22	8.2	0.09	0.09	<2	<2
			21.5		<0.1		9.03		102.4		0.65		8.22		0.09		<2	

**Water Quality Impact Monitoring Result for M3**

Date		1 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:10	2.39	17	17.0	<0.1	<0.1	8.7	8.68	93.4	93.2	0.73	0.7	7.23	7.2	0.01	0.01	4	4.0
			17		<0.1		8.65		92.9		0.7		7.23		0.01		4	

Date		3 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	11:10	2.37	18.6	18.4	<0.1	<0.1	8.49	8.50	94.5	94.6	0.13	0.1	7.60	7.6	0.01	0.01	4	4.0
			18.2		<0.1		8.5		94.6		0.12		7.60		0.01		4	

Date		6 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:15	2.38	17.5	17.5	<0.1	<0.1	8.37	8.36	95.0	94.9	1.72	1.8	7.19	7.2	0.01	0.01	2	2.5
			17.5		<0.1		8.35		94.8		1.84		7.19		0.01		3	

Date		8 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	0.625	2.39	18.7	18.7	<0.1	<0.1	8.38	8.38	94.9	94.9	2.04	2.1	7.13	7.1	0.01	0.01	2	2.5
			18.7		<0.1		8.37		94.8		2.06		7.13		0.01		3	

Date		10 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:10	2.37	18.8	18.8	<0.1	<0.1	8.3	8.29	93.9	93.8	1.22	1.2	7.37	7.4	0.01	0.01	2	2.5
			18.8		<0.1		8.28		93.6		1.21		7.37		0.01		3	

Date		13 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:10	2.35	19.7	19.7	<0.1	<0.1	8.23	8.23	94.5	94.4	0.44	0.4	7.70	7.7	0.01	0.01	<2	<2
			19.7		<0.1		8.22		94.3		0.42		7.70		0.01		<2	

Date		15 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:25	2.37	19.1	19.1	<0.1	<0.1	8.24	8.24	94.8	94.8	2.37	2.4	7.64	7.6	0.01	0.01	2	2.5
			19.1		<0.1		8.23		94.7		2.52		7.64		0.01		3	

Date		17 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:20	2.36	19.9	19.9	<0.1	<0.1	8.18	8.18	94.0	94.0	1.64	1.7	8.26	8.3	0.01	0.01	2	2.0
			19.9		<0.1		8.17		93.9		1.68		8.26		0.01		2	

Date		20 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:10	2.33	17.7	17.7	<0.1	<0.1	9.12	9.08	96.0	95.6	1.76	1.8	8.21	8.2	0.01	0.01	3	3.0
			17.7		<0.1		9.04		95.2		1.74		8.21		0.01		3	

Date		22 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:25	2.39	17.3	17.3	<0.1	<0.1	9.22	9.22	97.4	97.4	1.04	1.0	8.02	8.0	0.01	0.01	5	5.5
			17.3		<0.1		9.22		97.3		1.03		8.02		0.01		6	

Date		24 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	10:18	2.37	21.5	21.5	<0.1	<0.1	8.99	9.00	101.9	102.0	0.56	0.6	8.19	8.2	0.09	0.09	<2	<2
			21.5		<0.1		9		102.0		0.54		8.19		0.09		<2	

Date		27 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M3	9:49	2.38	21.2	21.2	<0.1	<0.1	8.89	8.90	100.3	100.4	1.34	1.3	8.07	8.1	0.05	0.05	2	2.0
			21.2		<0.1		8.91		100.4		1.33		8.07		0.05		2	

**Water Quality Impact Monitoring Result for M4**

Date	1 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:30	0.40	16.9	16.9	<0.1	<0.1	8.16	8.16	87.7	87.7	1.4	1.4	7.20	7.1	0.04	0.04	3	3.5
			16.9		<0.1		8.15		87.6		1.4		7.02		0.04		4	

Date	3 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	11:45	0.40	18.5	18.5	<0.1	<0.1	8.37	8.36	92.9	92.8	3.7	4.0	7.49	7.5	0.06	0.06	4	4.0
			18.5		<0.1		8.34		92.6		4.2		7.49		0.06		4	

Date	6 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:35	0.41	17.7	17.7	<0.1	<0.1	8.8	8.81	100.3	100.4	2.0	1.9	7.06	7.0	0.08	0.08	3	2.5
			17.7		<0.1		8.81		100.4		1.9		7.03		0.08		2	

Date	8 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:45	0.43	19	19.0	<0.1	<0.1	8.75	8.76	98.9	99.0	1.1	1.1	7.05	7.1	0.06	0.06	2	2.0
			19		<0.1		8.77		99.0		1.1		7.05		0.06		2	

Date	10 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:30	0.42	19.1	19.1	<0.1	<0.1	8.73	8.73	98.5	98.6	1.1	1.1	7.17	7.2	0.08	0.08	2	2.0
			19.1		<0.1		8.73		98.6		1.1		7.17		0.08		2	

Date	13 Feb 23																	
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:30	0.42	20	20.0	<0.1	<0.1	8.53	8.54	97.9	98.0	0.9	0.9	7.56	7.6	0.09	0.09	<2	<2
			20		<0.1		8.54		98.0		0.9		7.56		0.09		<2	

Date		15 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:45	0.40	19.2	19.2	<0.1	<0.1	8.56	8.56	98.6	98.7	1.1	1.1	7.66	7.7	0.09	0.09	<2	<2
			19.2		<0.1		8.56		98.7		1.1		7.66		0.09		<2	

Date		17 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:40	0.41	20.1	20.1	<0.1	<0.1	8.34	8.34	95.8	95.8	2.7	2.7	8.13	8.1	0.09	0.09	<2	<2
			20.1		<0.1		8.34		95.7		2.7		8.13		0.09		<2	

Date		20 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:30	0.40	18.2	18.2	<0.1	<0.1	13.51	13.57	140.5	141.1	1.4	1.4	7.68	7.7	0.04	0.04	4	3.5
			18.2		<0.1		13.62		141.7		1.4		7.69		0.04		3	

Date		22 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:45	0.41	17.8	17.8	<0.1	<0.1	13.12	13.12	137.2	137.1	1.5	1.5	7.36	7.4	0.06	0.06	3	3.0
			17.8		<0.1		13.11		137.0		1.5		7.36		0.06		3	

Date		24 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	9:20	0.42	18.6	18.6	<0.1	<0.1	8.8	8.79	97.3	97.2	5.5	5.3	8.29	8.3	0.05	0.05	4	4.5
			18.6		<0.1		8.78		97.1		5.1		8.29		0.05		5	




Date		27 Feb 23																
Location	Time	Depth (m)	Temp (oC)		Flow Velocity (m/s)		DO (mg/L)		DO (%)		Turbidity (NTU)		pH		Salinity		SS(mg/L)	
M4	10:45	0.40	17	17.0	<0.1	<0.1	8.2	8.17	90.3	90.0	1.3	1.3	7.02	7.0	0.05	0.05	3	3.5
			17		<0.1		8.14		89.7		1.4		7.02		0.05		4	

## **Appendix I**




### **Graphical Plots of Air Quality, Noise and Water Quality**





### Air Quality Impact Monitoring – 1-hour TSP

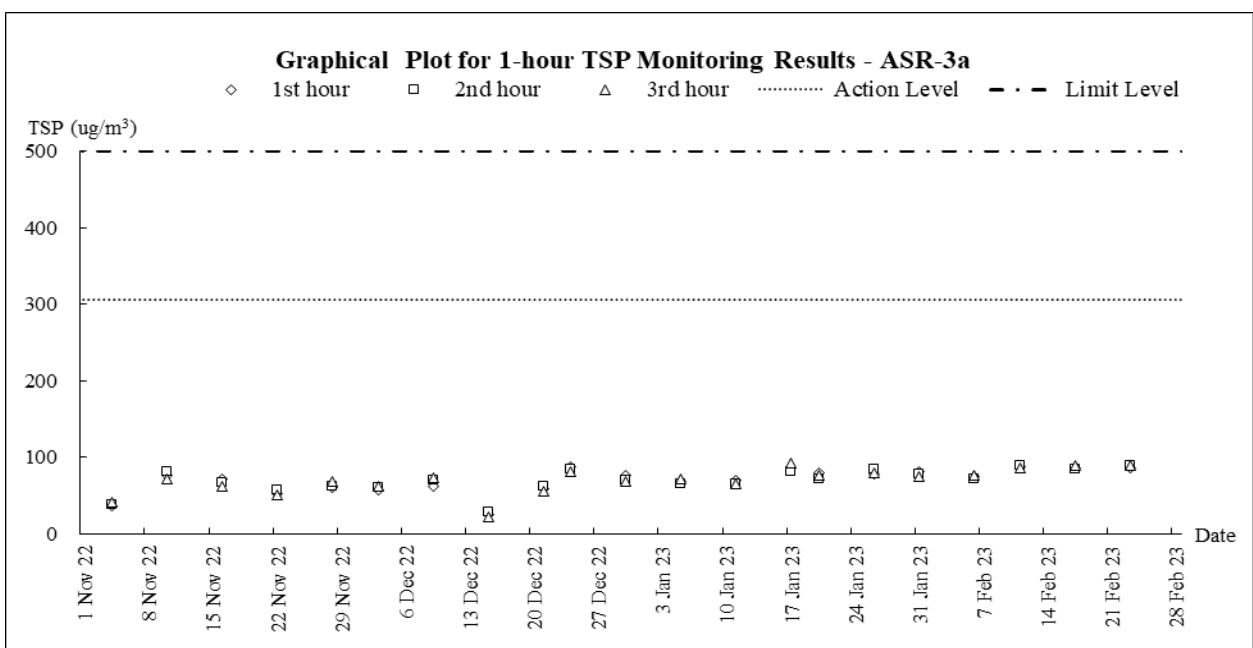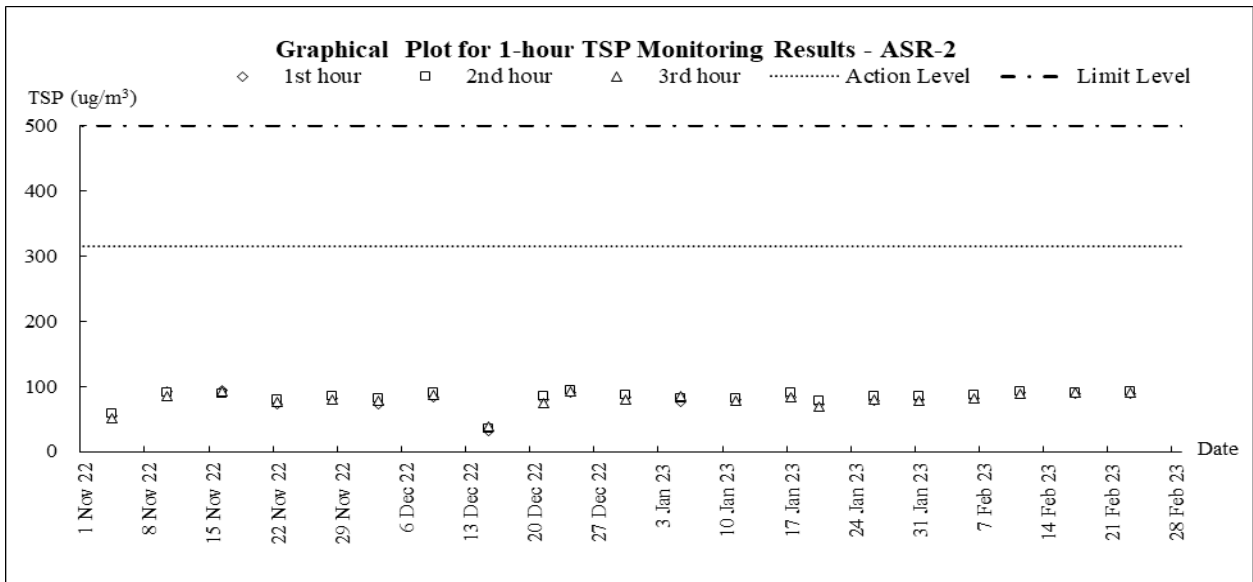
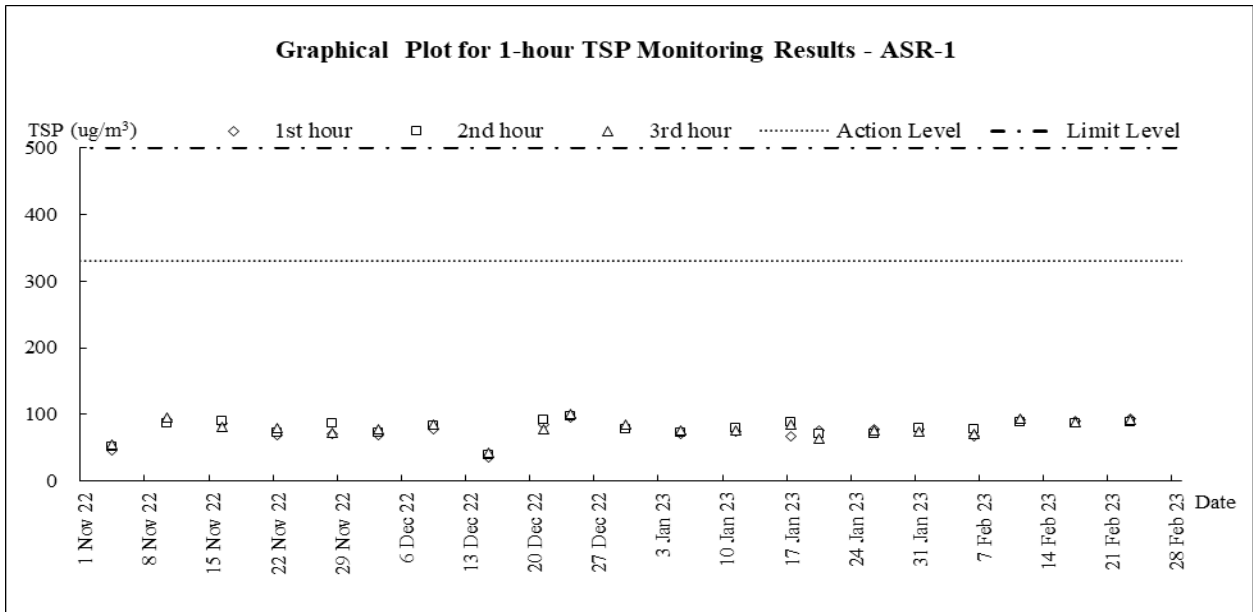


### Air Quality Impact Monitoring – 24-hour TSP

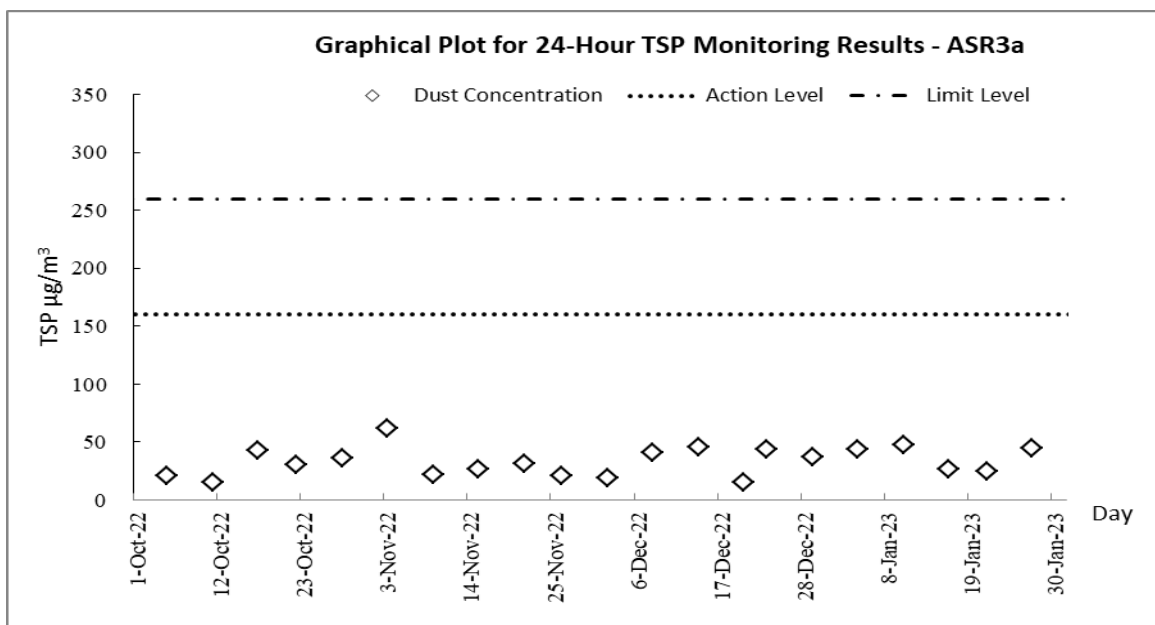
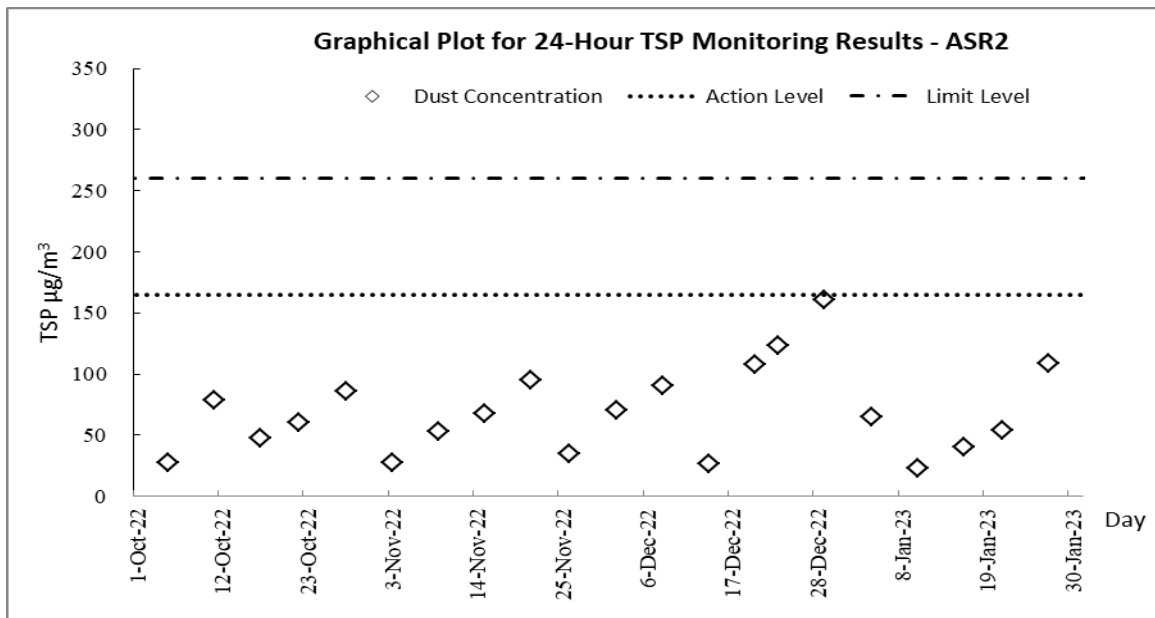
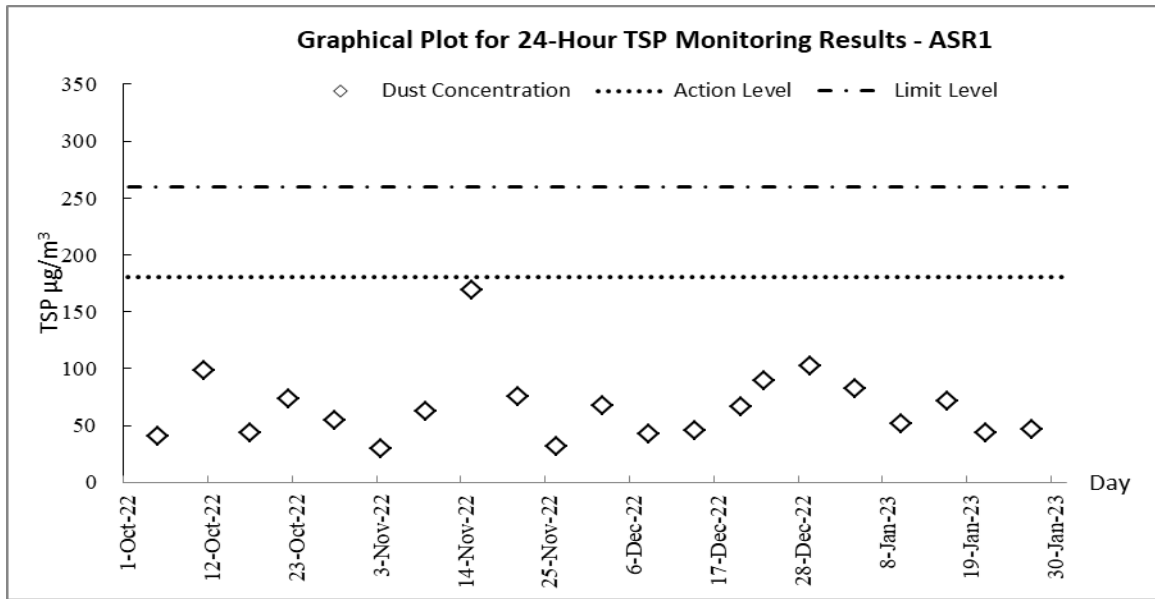





### Construction Noise Impact Monitoring


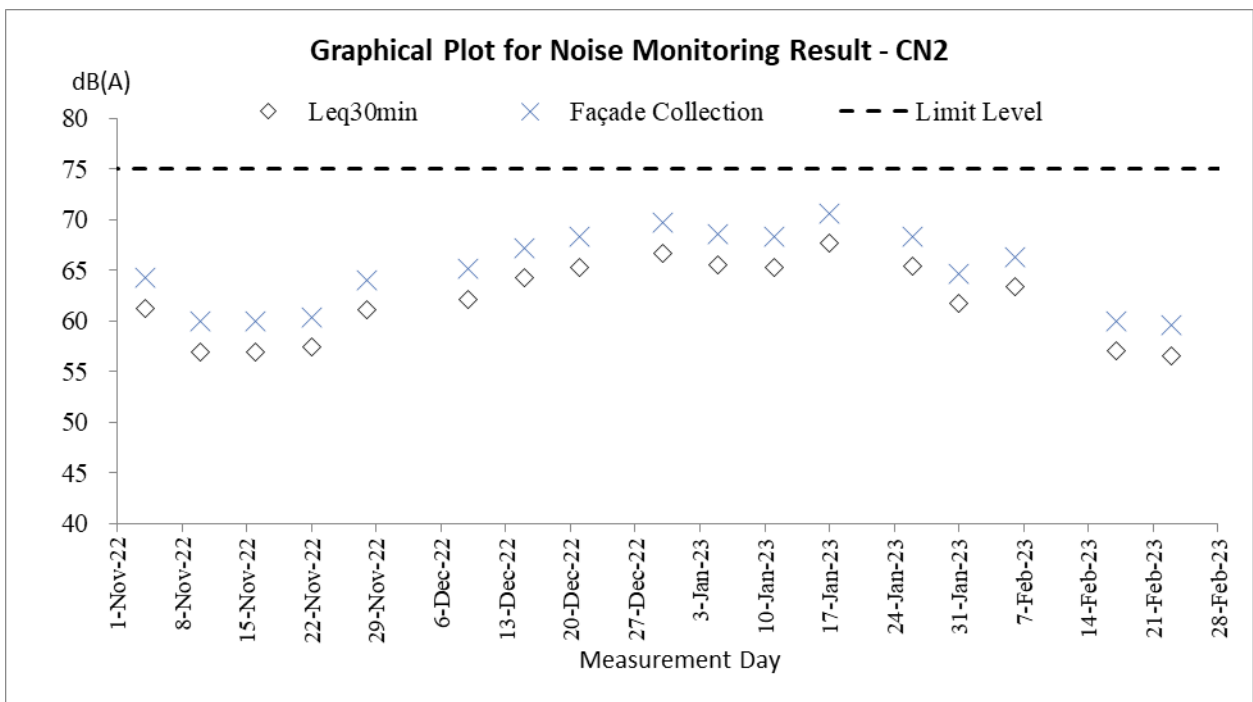
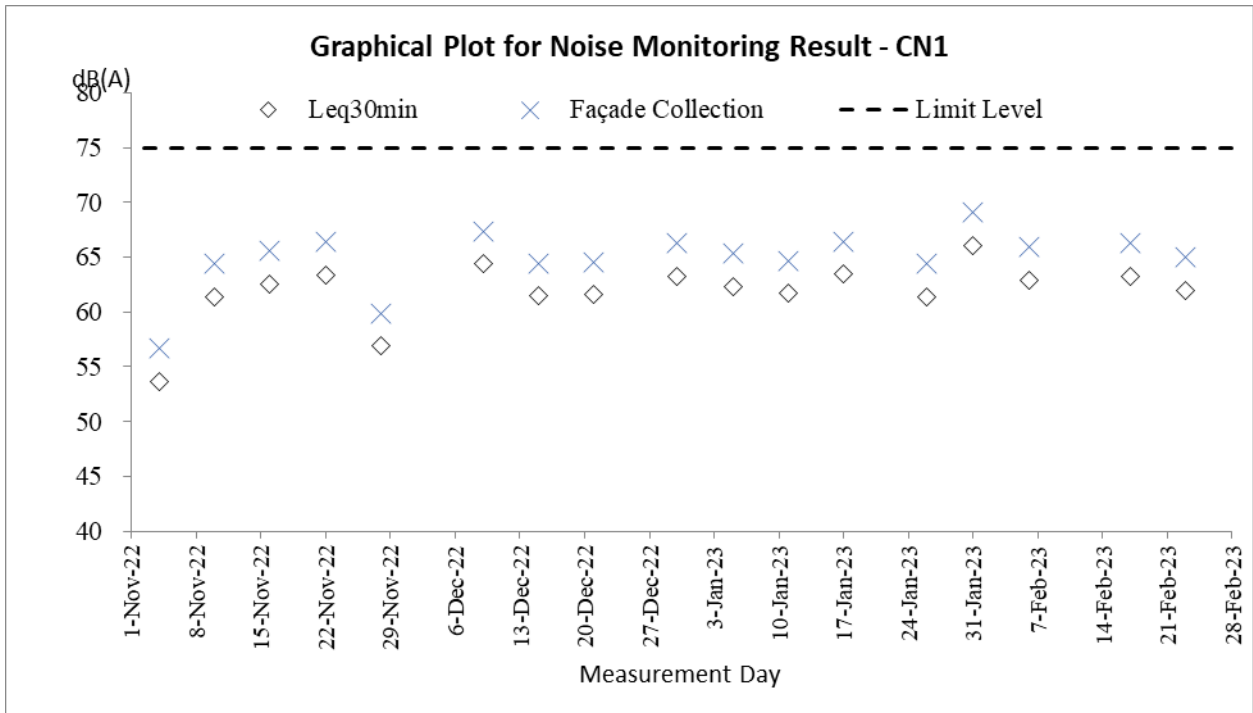


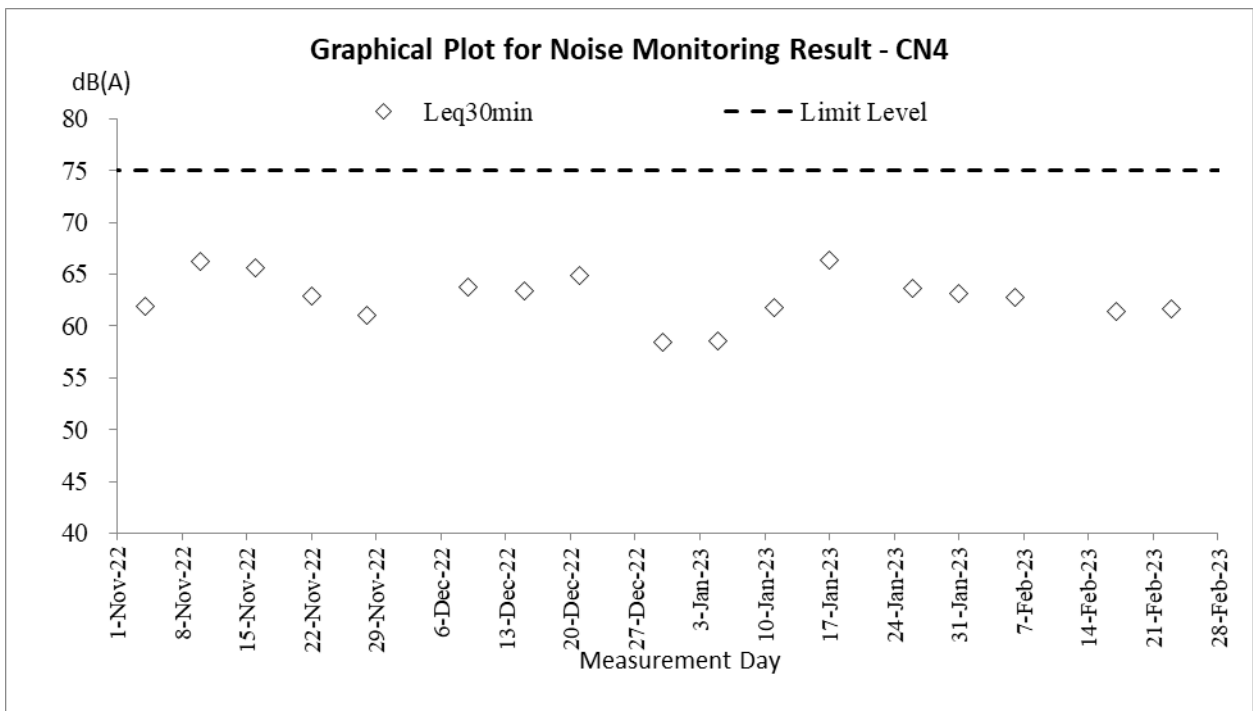
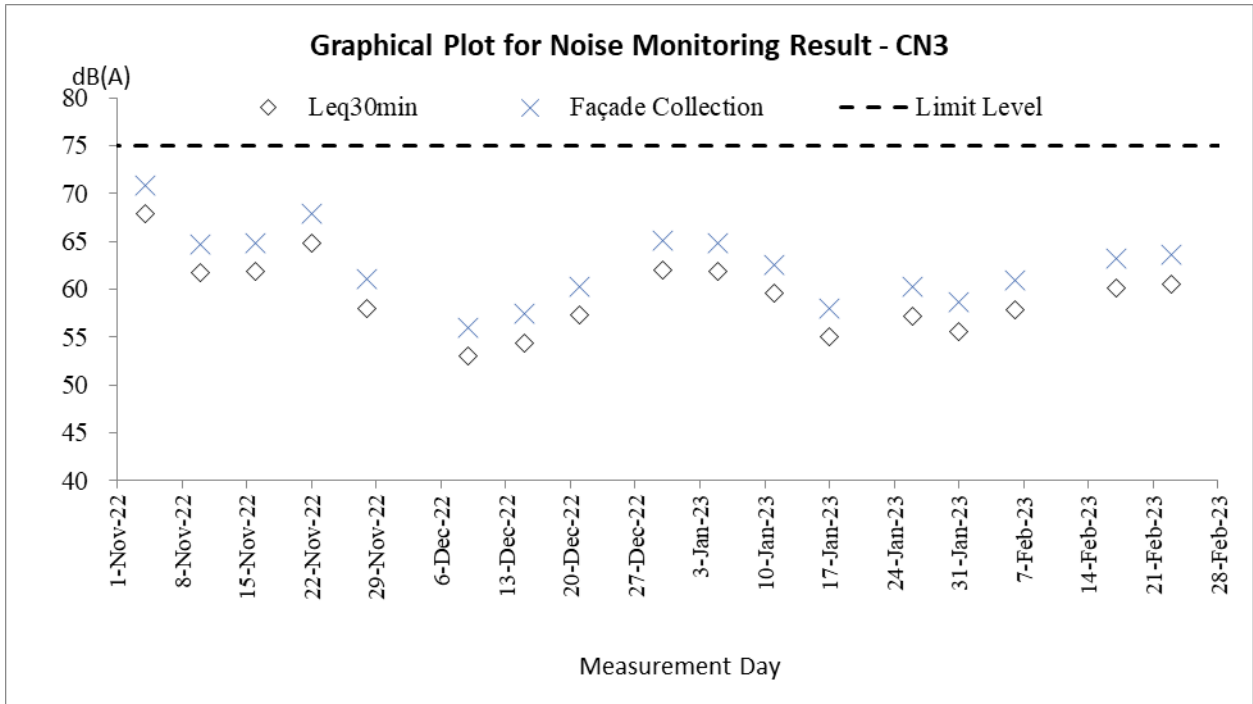


### Water Quality Impact Monitoring

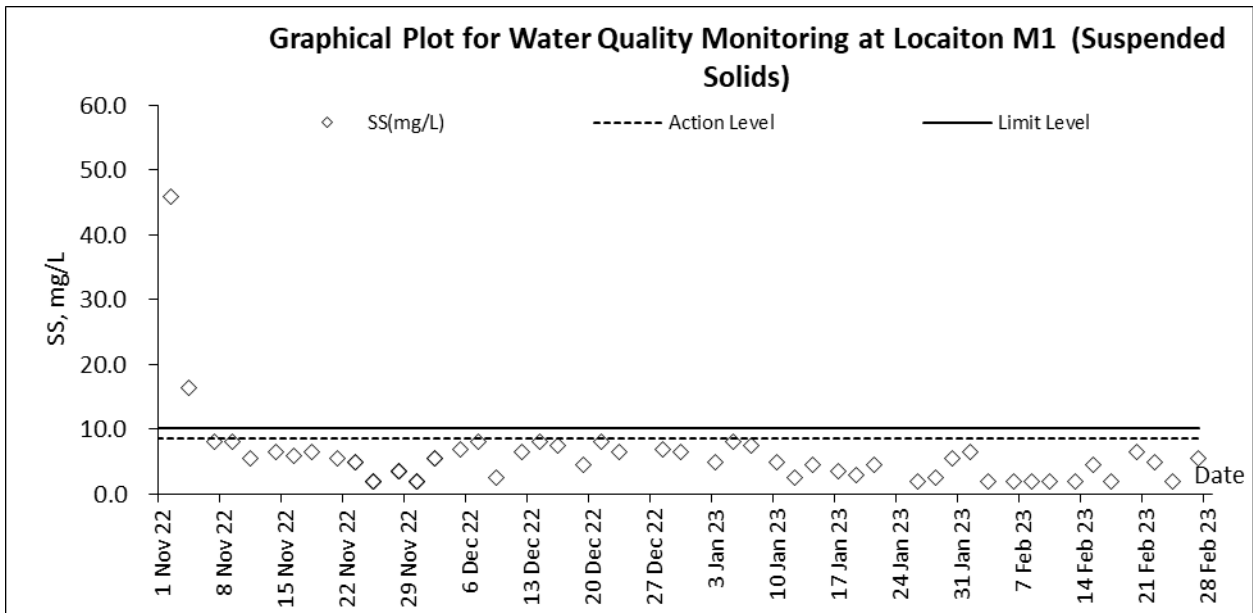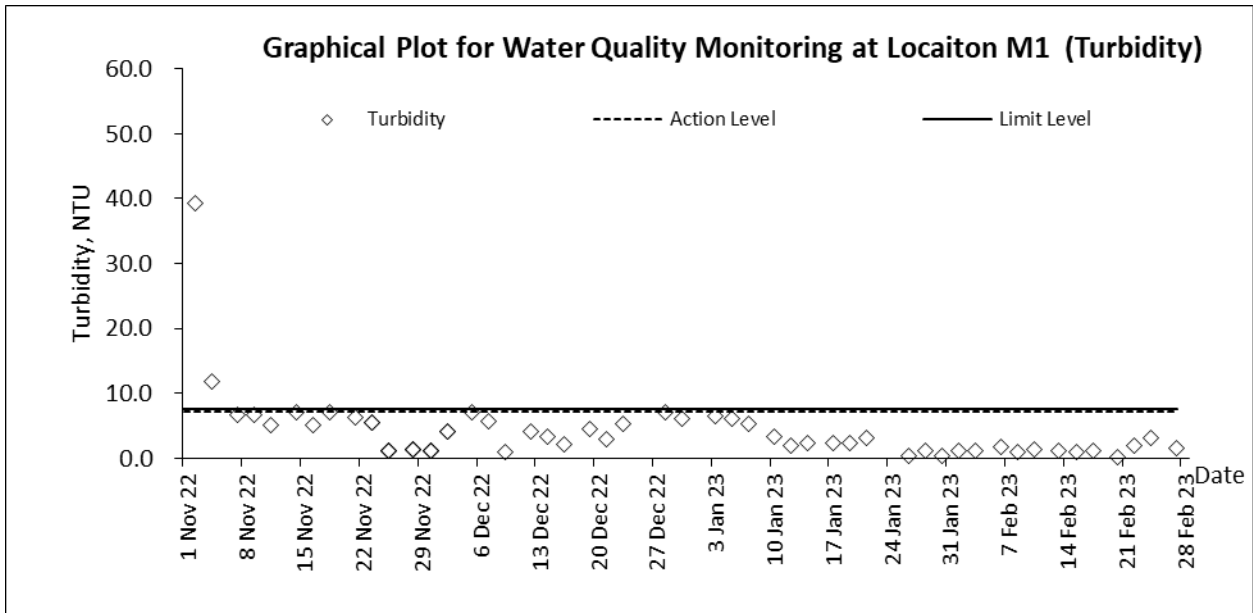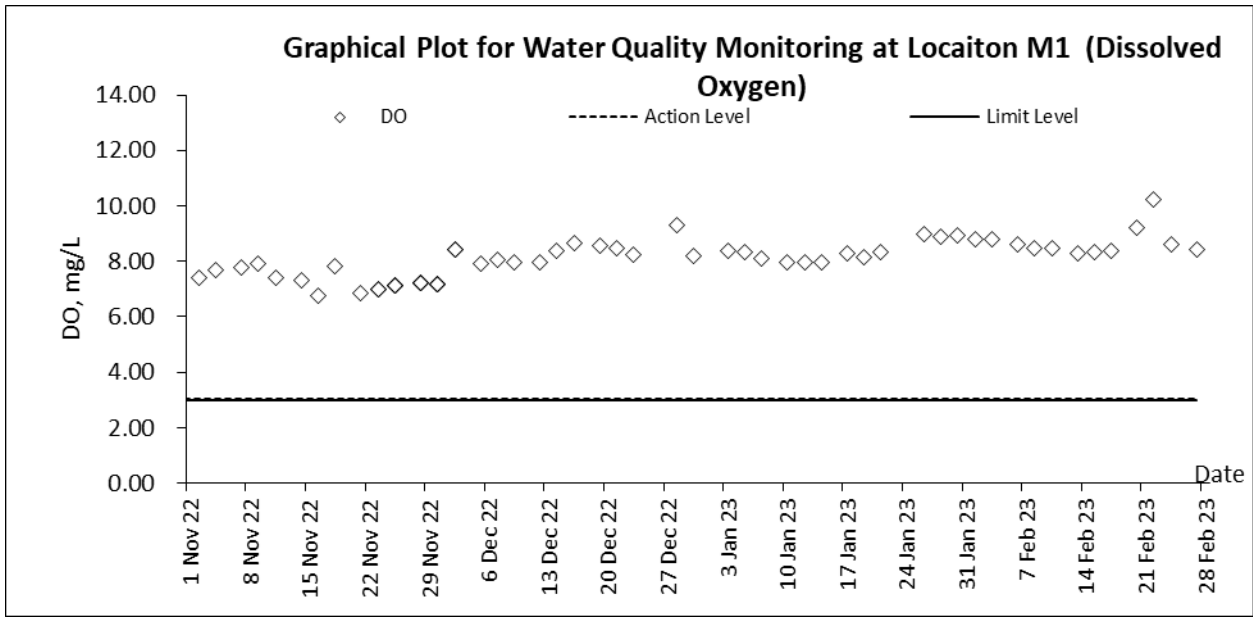


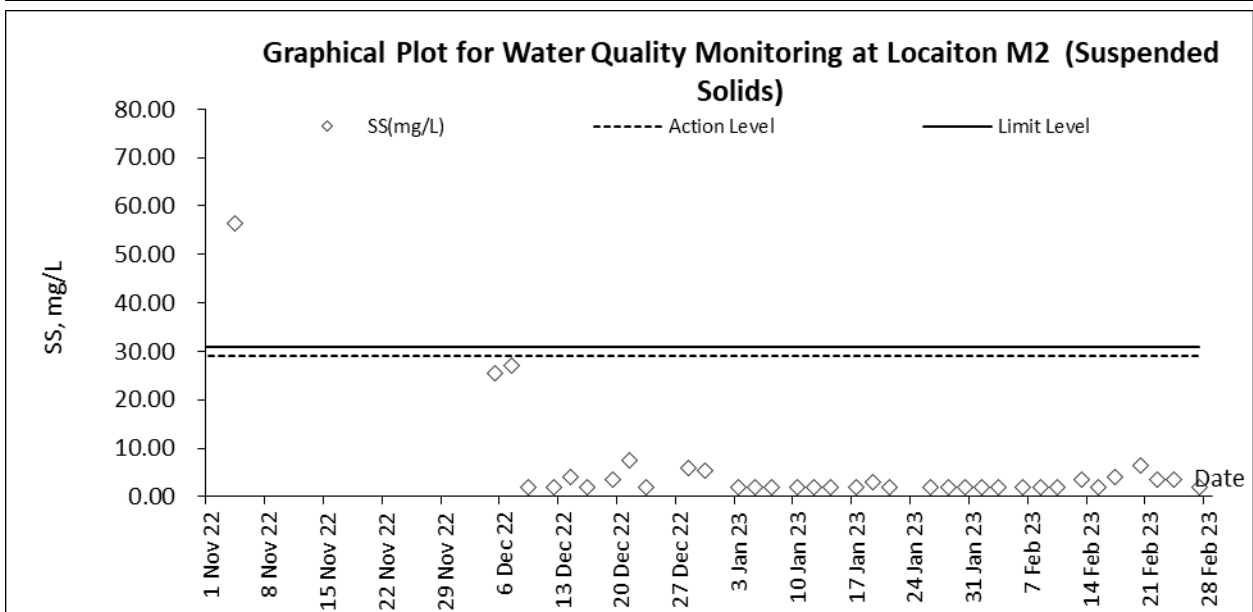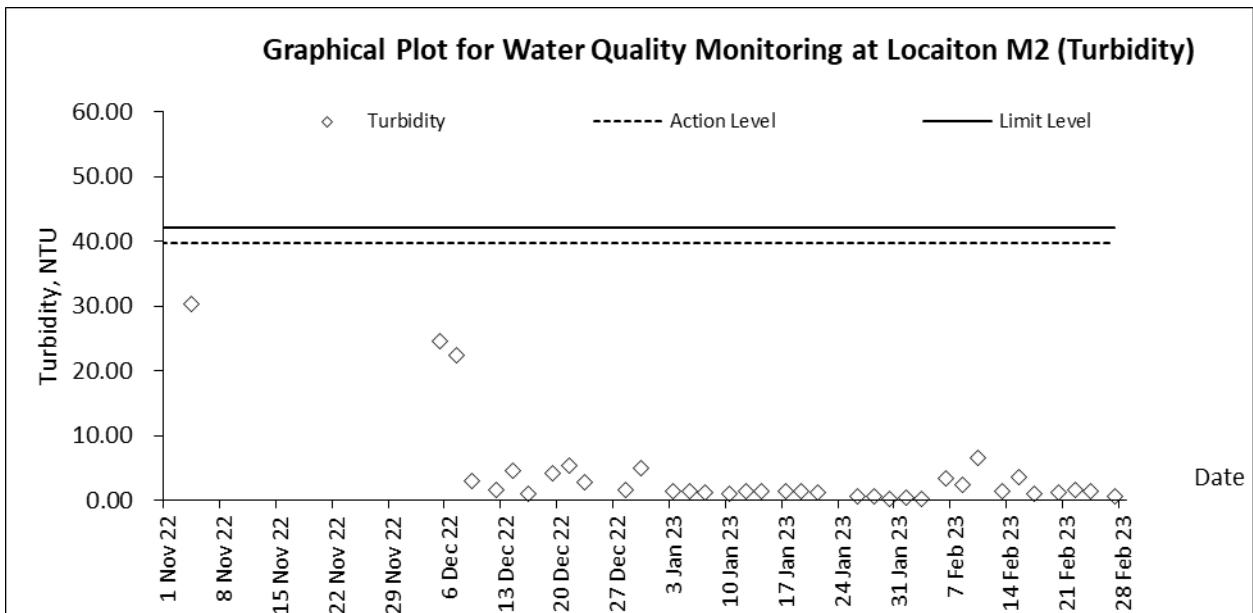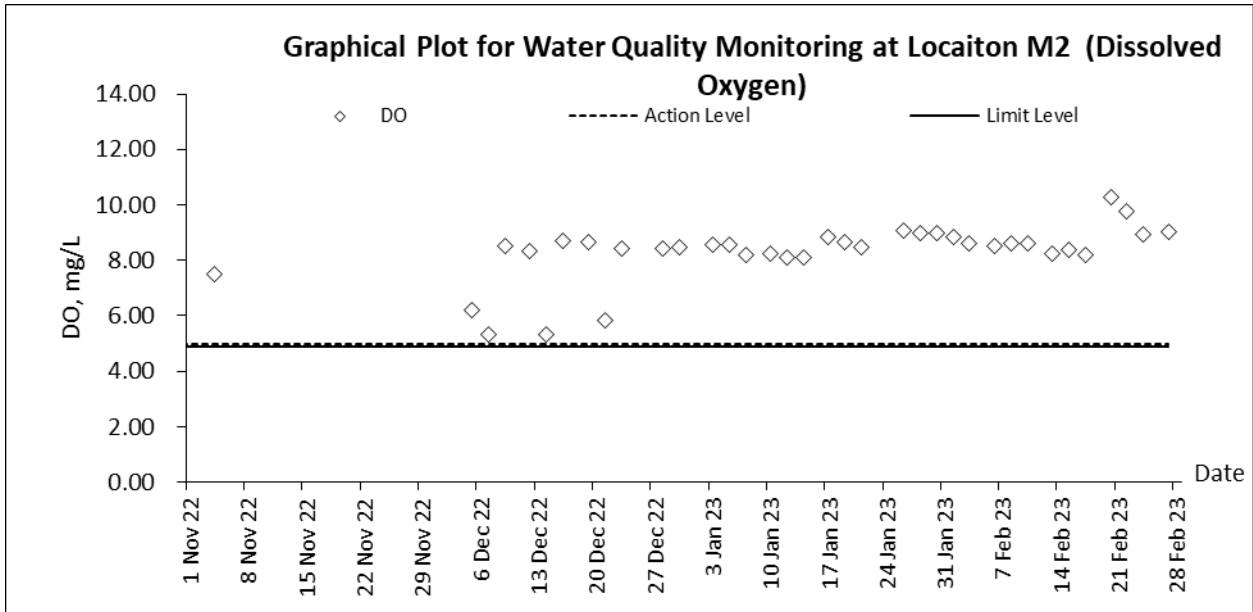

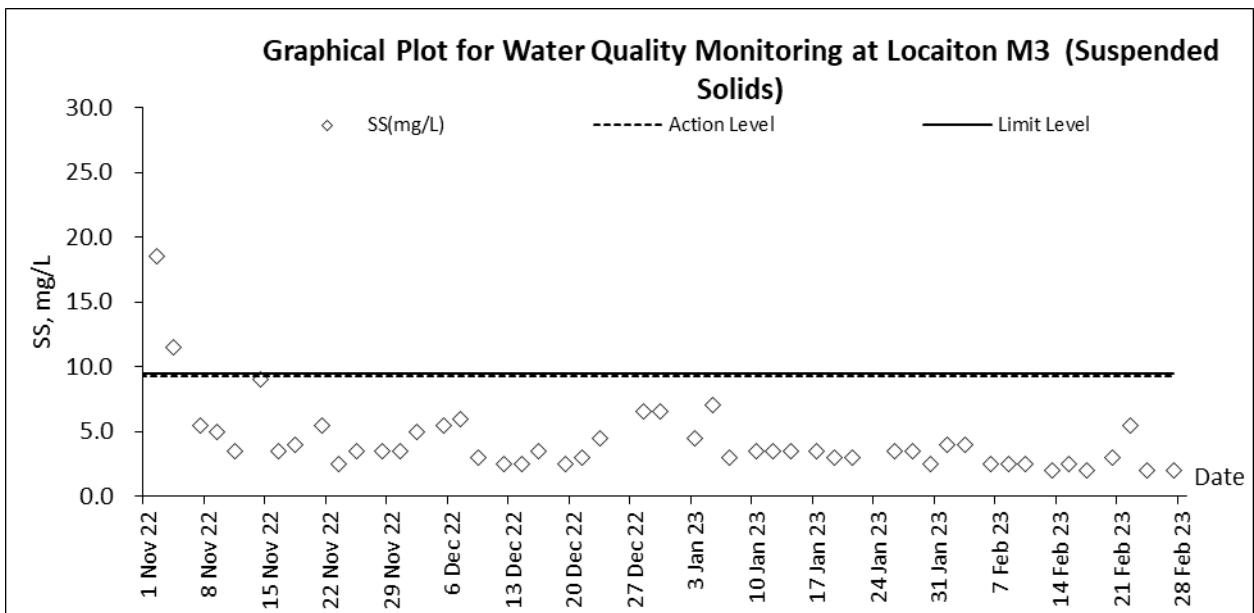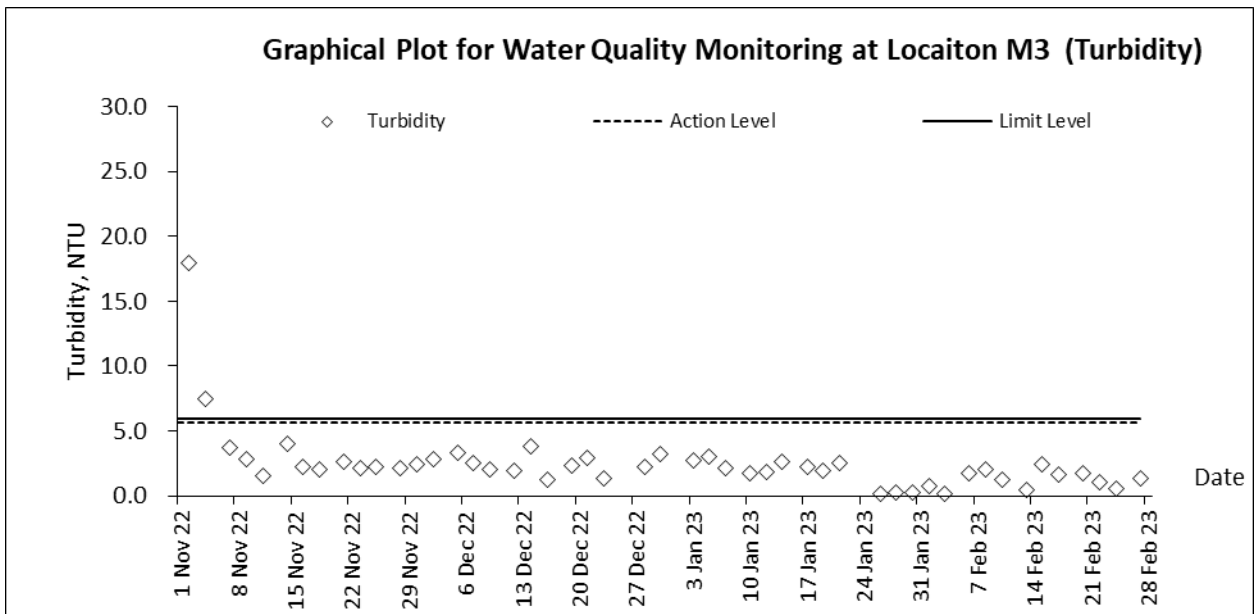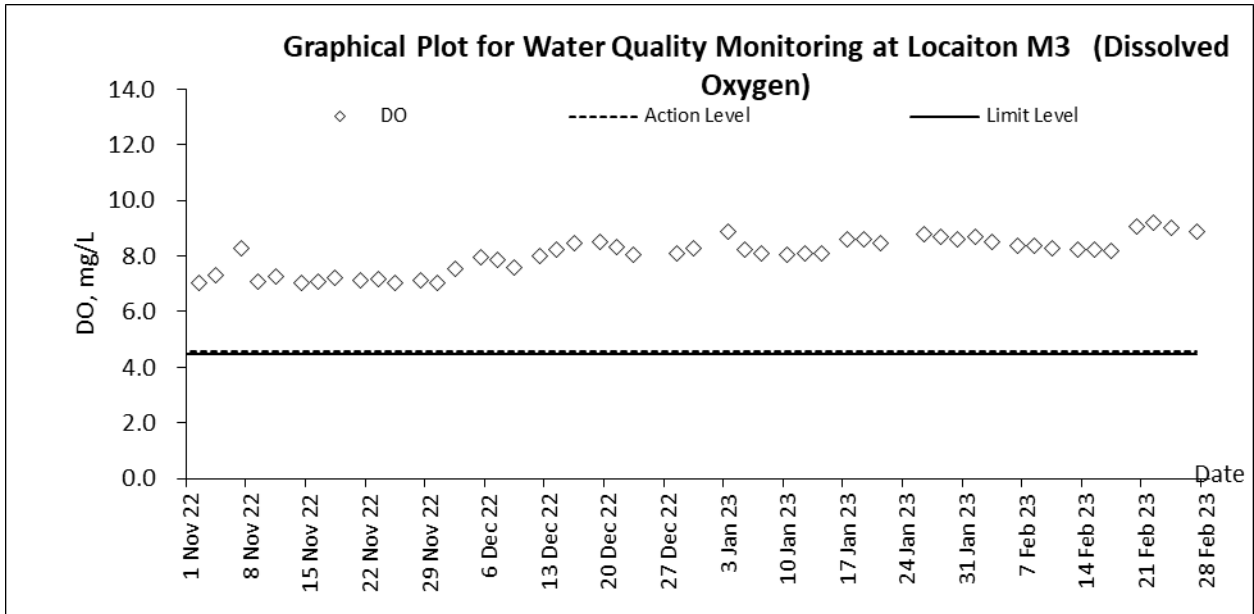

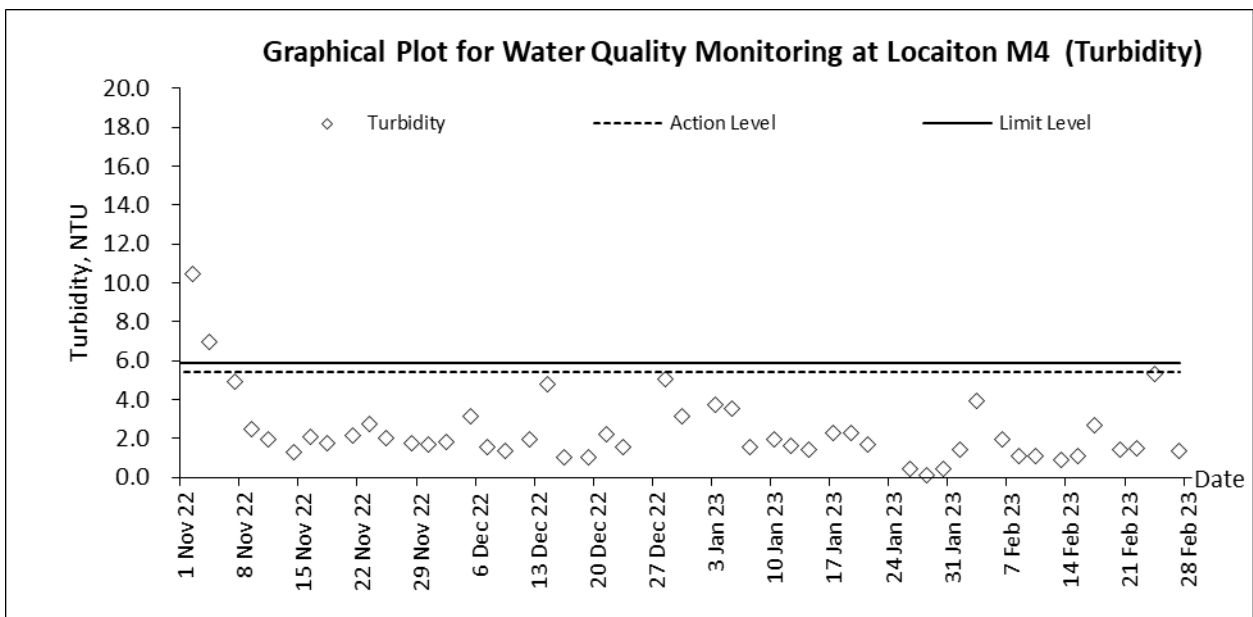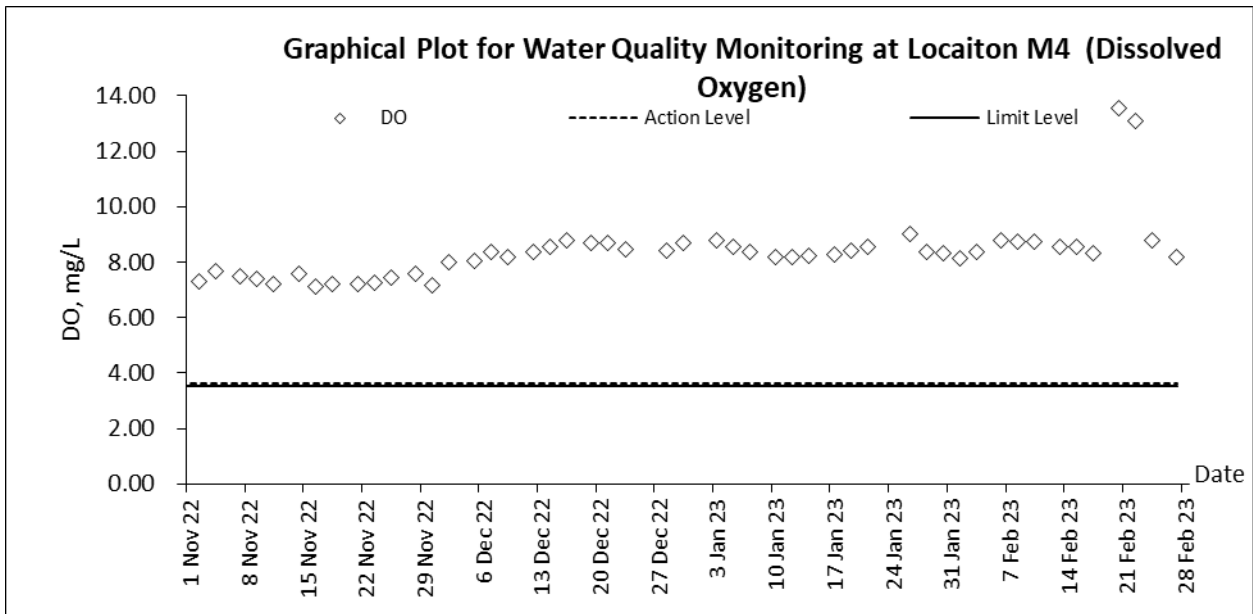



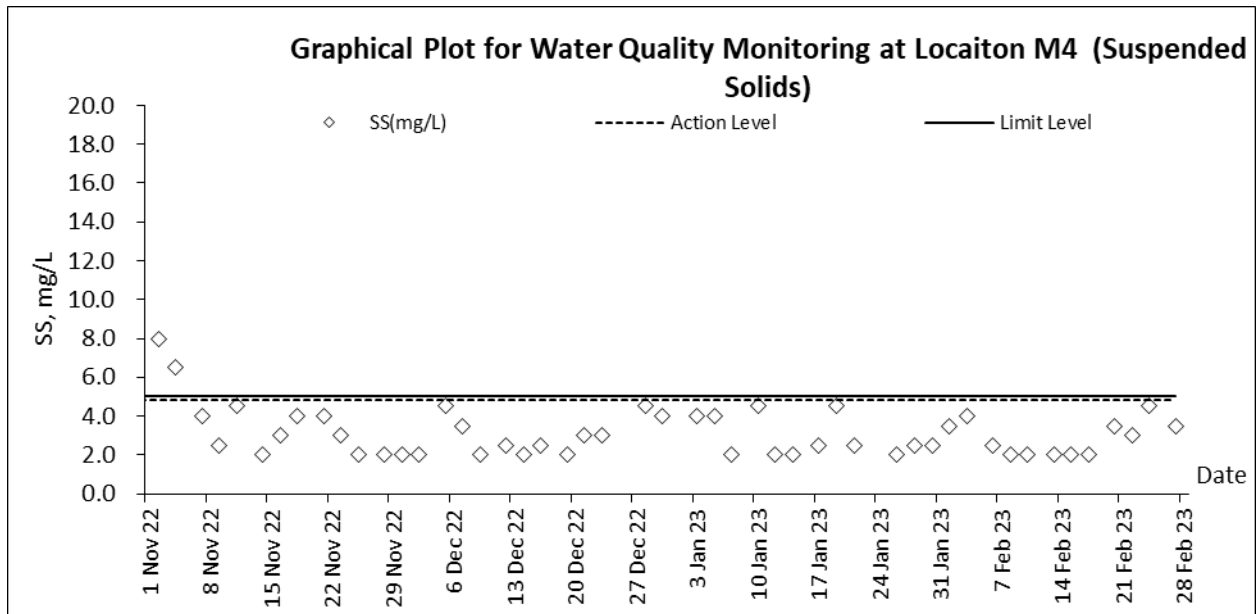

## **Appendix J**

### **Meteorological Data of the Reporting Month**

Date		Weather	Total Rainfall (mm)	Ta Kwu Ling Station			
				Mean Air Temp. (°C)	Wind Speed (km/h)	Mean Relative Humidity (%)	Wind Direction
1-Jan-23	Sun	Dry with sunny periods tomorrow.	0.1	13.2	9.2	61.0	N
2-Jan-23	Mon	Becoming cloudy	Trace	17.7	8	64.0	N
3-Jan-23	Tue	Mainly fine and dry.	Trace	15.7	11.5	69.0	N/NE
4-Jan-23	Wed	Moderate north to northeasterly winds	Trace	16.8	6.2	70.0	N/NE
5-Jan-23	Thu	Moderate north to northeasterly winds	0	19.7	6.2	70.5	N
6-Jan-23	Fri	Cloudy with a few rain patches.	0	18.5	11.2	67.7	N/NE
7-Jan-23	Sat	Moderate east to northeasterly winds	0	17.7	8.5	68.0	N/NE
8-Jan-23	Sun	Cloudy with a few rain patches.	Trace	17.8	6	69.0	E/SE
9-Jan-23	Mon	Moderate to fresh east to northeasterly winds	0.1	18.5	5.5	78.5	N
10-Jan-23	Tue	Cloudy with one or two rain patches.	5.5	17.4	5	90.0	N
11-Jan-23	Wed	Moderate to fresh east to northeasterly winds.	3.2	17.7	5	90.7	E
12-Jan-23	Thu	Mainly cloudy with coastal fog.	0.5	18.7	13.2	88.2	E/SE
13-Jan-23	Fri	One or two light rain patches.	4.5	21.4	8	91.0	E/SE
14-Jan-23	Sat	Light to moderate southeasterly winds.	3.4	23.7	6.2	83.0	W
15-Jan-23	Sun	Sunny intervals in the afternoon.	Trace	15.1	20	69.2	N/NE
16-Jan-23	Mon	It will be cold. Mainly cloudy and dry.	0	9.8	18.5	63.5	N/NE
17-Jan-23	Tue	Cold and mainly cloudy.	0	10.8	8.5	71.5	N
18-Jan-23	Wed	Fine and dry. Moderate northeasterly winds.	0	Maintenance	13.2	Maintenance	N
19-Jan-23	Thu	Fine. Dry in the afternoon.	0	13.0	6.2	68.2	N
20-Jan-23	Fri	Moderate northeasterly winds	Trace	16.1	6	66.7	N/NW
21-Jan-23	Sat	Moderate northeasterly winds	Trace	17.1	7.2	65.2	N/NE
22-Jan-23	Sun	Dry with sunny intervals during the day.	0.6	20.6	7.5	78.0	E/SE
23-Jan-23	Mon	<u>Mainly cloudy.</u>	0	18.6	9	81.0	E/SE
24-Jan-23	Tue	Mainly cloudy.	0.3	13.9	19.5	50.7	N/NE
25-Jan-23	Wed	Bright periods during the day.	0	11.5	8.7	63.7	E/NE
26-Jan-23	Thu	Moderate to fresh east to northeasterly winds.	0	12.7	6.2	71.2	E/SE
27-Jan-23	Fri	<u>Cold in the morning and at night.</u>	0	13.9	15	58.5	N/NE
28-Jan-23	Sat	Moderate to fresh north to northeasterly winds	0	10.2	13.7	45.5	N/NE
29-Jan-23	Sun	Fine and very dry at first.	0	10.6	10.1	51.5	N/NW
30-Jan-23	Mon	Sunny intervals during the day	0	11.7	7.5	57.0	E/SE
31-Jan-23	Tue	Sunny periods. Mainly cloudy tonight.	0	15.6	8	66	E

## **Appendix K**

### **Ecological Survey Report**




## **Ecological Survey Report for Contract CV/2016/10**

## **Contract No. CV/2016/10**

# **Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery**

---

## **Monthly Report of Ecologically Sensitive Habitats Monitoring – February 2023**

Revision	0	
Date of issue	1 March 2023	
Prepared by	Alan Lam	
Reviewed by	Rachel Siu	
Verified by	Mike Leung	

## Table of Contents

<b>1</b>	<b>INTRODUCTION</b>	<b>4</b>
1.1	BACKGROUND	4
1.2	OBJECTIVE	4
<b>2</b>	<b>ECOLOGICALLY SENSITIVE HABITATS</b>	<b>5</b>
2.1	DESCRIPTION OF HABITATS	5
2.2	MONITORING MEASURES OF WETLAND HABITATS	6
2.3	MONITORING MEASURES OF NON-WETLAND HABITATS	6
<b>3</b>	<b>METHODOLOGY</b>	<b>7</b>
3.1	MAMMAL SURVEY	7
3.2	BIRD SURVEY	7
3.3	HERPETOFAUNA SURVEY	7
3.4	DRAGONFLY SURVEY	7
3.5	BUTTERFLY SURVEY	8
3.6	AQUATIC FAUNA SURVEY	8
<b>4</b>	<b>RESULT</b>	<b>9</b>
<b>5</b>	<b>DISCUSSION</b>	<b>13</b>
	<b>Appendix I – Transect Routes for Contract CV/2016/10</b>	<b>16</b>

<b><u>LIST OF TABLE</u></b>	
Table 1	Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna
Table 2	Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna
Table 3	Survey Schedule
Table 4	Result of mammal in survey
Table 5	Result of Avifauna in survey
Table 6	Result of reptile in survey
Table 7	Result of amphibian in survey
Table 8	Result of butterfly in survey
Table 9	Result of Odonate in survey
Table 10	Result of freshwater communities in survey

<b><u>LIST OF APPENDIX</u></b>	
Appendix I	Transect Routes for Contract CV/2016/10

<b><u>LIST OF FIGURES</u></b>	
Figure 1	Bar chart showing the total species richness within site boundary from 2019 to 2023
Figure 2	Bar chart showing the total abundance within site boundary from 2019 to 2023
Figure 3	Bar chart showing the species richness within site boundary by taxa from 2019 to 2023
Figure 4	Bar chart showing the species richness based on habitat type from 2019 to 2023
Figure 5	Bar chart showing the abundance based on habitat type from 2019 to 2023



# 1 INTRODUCTION

## 1.1 BACKGROUND

- 1.1.1 The main objective of the proposed site formation and associated infrastructural works for development of columbarium, crematorium (C&C) and related facilities at Sandy Ridge Cemetery is to increase the public cremation services and supply of public niches to meet the future demand.
- 1.1.2 The project includes site formation and associated works for development of C&C facilities at the Sandy Ridge Cemetery, road works within Sandy Ridge Cemetery, widening a section of Lin Ma Hang Road (from 6.5m to 7.3m), provision of off-site pick-up/drop-off points for shuttle buses as well as barging point at Siu Lam, Lok On Pai.
- 1.1.3 The Environmental Impact Assessment (EIA) report, including Environmental Monitoring and Audit Manual (EM&A Manual), was approved with conditions on 8 August 2016 (Register No.: AEIAR-198/2016). EPD issued an Environmental Permit (EP) for the Project (EP-534/2017) on 7 April 2017. A Further Environment Permit (FEP) for the Project (FEP-01/534/2017) was issued on 23 February 2018, variation of EP (EP-534/2017/A) and variation of FEP (FEP-01/534/2017/A) were issued on 24 December 2018.
- 1.1.4 According to Clause 3.1 of the FEP (FEP-01/534/2017/A), “The Permit Holder shall implement the EM&A programme in accordance with the procedures and requirements as set out in the EM&A Manual. Any changes to the programme shall be justified by the ET Leader and verified by the IEC as conforming to the information and requirements contained in the EM&A Manual before submission to the Director for approval”.
- 1.1.5 This Ecologically Sensitive Habitats Monitoring Methodology articulates the protocol of monitoring the ecology of concerned habitats as specified in EM&A Manual.

## 1.2 OBJECTIVE

- 1.2.1 According to approved EIA report (AEIAR-198/2016), habitat types within project boundary comprise of watercourse, grassland, upland grassland, plantation, woodland and developed area. Natural habitats were of moderate ecological value in terms of species diversity, species rarity, species abundance, ecological linkage as well as nursery. Moreover, 0.3ha of wet woodland on the northern side of Sandy Ridge was deemed habitat with high ecological value. Four types of habitats were regarded as ecologically sensitive habitats, namely wet woodland, watercourses, upland grassland and woodland. Considering human disturbance in upcoming construction and operation phases, ecologically sensitive habitats shall be monitored in accordance with EM&A Manual.
- 1.2.2 The objective of ecologically sensitive habitats monitoring is to evaluate the effectiveness of measures to minimize impacts on concerned habitats from disturbance and pollution.

## 2 ECOLOGICALLY SENSITIVE HABITATS

### 2.1 DESCRIPTION OF HABITATS

2.1.1 In order to monitor the effectiveness of the measures to the minimise impact on ecologically sensitive habitats from disturbance and pollution, monthly monitoring during construction and operation phases is required as specified in EM&A Manual. Standard faunal transect and sampling surveys cover both wetland and non-wetland habitats:

Wetland habitats	Non-wetland habitats
Wet Woodland Watercourses	Upland Grassland Woodland

2.1.2 Wet woodland is small patch present on northwest of the project boundary, and is confined by the marsh area to the north and the secondary woodland to the east, south and south-west parts. A number of mature trees *Cleistocalyx nervosum* and *Acronychia pedunculata* form the tree canopy, with other self-sown shrubs (including *Psychotria asiatica*, *Ligustrum sinense* and *Glochidion lanceolarium*) and trees (*Aporosa dioica* and *Litsea monopetala*). Whilst botanically it comprises of naturally regenerated secondary woodland and ground level are a series of small braided streams and weep points which even during the dry season remain wet. This creates a rather uncommon habitat in Hong Kong offering suitable conditions for a good assemblage of common wetland species. The wet woodland provides a good assemblage of micro-habitats, which is relatively undisturbed and has good linkages to other natural habitats. Several species of conservation importance were recorded in EIA report from this habitat: East Asian Porcupine, Leopard Cat, Red Muntjac, Two-striped Grass Frog, Small Snakehead, *Somanniathelphusa zanklon*, Dancing Shadow-emerald.

2.1.3 Seasonal watercourse running west to east in the eastern part of the area inside the Project boundary is shallower in gradient than those running off the hillside. This seasonal watercourse is heavily vegetated with wetland-associated herbs including *Commelina diffusa*, *Polygonum chinense*, *Colocasia esculenta* and *Dracaena sanderiana*. A mature tree of *Aquilaria sinensis* was recorded at the bank of the seasonal watercourse to the west of the Sandy Ridge Cemetery Office. Seasonal watercourses are restricted to the steeper slopes within the project boundary and are characterised by being entirely dry for much of the dry season. However, endemic crab *S. zanklon* population is supported by ephemeral watercourses close to the project boundary.

2.1.4 Upland grassland is the major habitat within the project boundary. The semi-natural habitat is dominated by typical upland grassland species: fern *Dicranopteris pedata*, grass *Neyraudia reynaudiana*, *Miscanthus floridulus*, climbing vines *Smilax china*, *Smilax glabra*, and shrubs such as *Rhodomyrtus tomentosa*, *Breynia fruticosa* and *Helicteres angustifolia*. Approximately 30 flowering spikes of two orchid species Bamboo Orchid and Toothed Habenaria were recorded near the hill top in the northern part of this upland grassland. Golden-headed Cisticola, which is considered as Local Concern by Fellowes *et al.* (2002), was also recorded in upland grassland on Sandy Ridge, including a proved breeding record of fledged young in September 2013. In addition, numerous species of conservation interest were recorded in EIA report, such as East Asian Porcupine, Leopard Cat, Red Muntjac, Great Swift, Tamil Grass Dart, Small Three-ring and Small Grass Yellow.

2.1.5 Scattered patches of woodland are present throughout the assessment area, with the largest contiguous block located immediately to the east of the project boundary. These woodlands are relatively young with single-layered of canopy dominants (~10 – 15m tall) including *A. dioica*, *Bridelia tomentosa*, *Cinnamomum burmannii*, *Daphniphyllum calycinum*, *Litsea glutinosa*, *Rhus succedanea*, and *Zanthoxylum avicennae*. Such areas comprise secondary woodland which is largely derived from natural regeneration and colonisation of trees as a result of seed dispersal by birds and/or bats. A mature tree of *A. sinensis* is located at the woodland edge at the central part of the Project according to EIA report.

## 2.2 MONITORING MEASURES OF WETLAND HABITATS

2.2.1 Wetland habitats include wet woodland and watercourses. Monitoring surveys using standardised quantitative methodology will be conducted at fixed points. For seasonal watercourse, survey shall be conducted whenever the habitat appears.

2.2.2 Measures to respond to decreases in numbers of aquatic fauna using the wetland habitats and action and limit levels to trigger these measures are detailed in Table 1.

Action Level	Response	Limit Level	Response
Reduction in taxa diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in taxa diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

Table 1 Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna

## 2.3 MONITORING MEASURES OF NON-WETLAND HABITATS

2.3.1 Non-wetland habitats consist of upland grassland and woodland. Monthly quantitative surveys of non-aquatic fauna will be conducted using standard route transect counts.

2.3.2 Measures to respond to decreases in numbers of non-aquatic fauna using the non-wetland habitats and action and limit levels to trigger these measures are detailed in Table 2.

Action Level	Response	Limit Level	Response
Reduction in species diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in species diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

Table 2 Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna

### 3 METHODOLOGY

The ecological survey includes all taxa being investigated in EIA report. Table 3 summarizes schedule of faunal surveys.

Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Mammals	√	√	√	√	√	√	√	√	√	√	√	√
Birds (day)	√	√	√	√	√	√	√	√	√	√	√	√
Birds (night)				√	√	√	√	√	√	√		
Herpetofauna				√	√	√	√	√	√	√		
Dragonflies			√	√	√	√	√	√	√	√		
Butterflies			√	√	√	√	√	√	√	√		
Aquatic fauna	√	√	√	√	√	√	√	√	√	√	√	√

Table 3 Survey Schedule

#### 3.1 MAMMAL SURVEY

3.1.1 Mammal surveys will be conducted along the transects shown in Appendix 1 during both daytime and night time periods. Along with direct observations, other field signs, such as scats and tracks, will be searched and recorded if present.

#### 3.2 BIRD SURVEY

3.2.1 Bird surveys will be conducted along the transects shown in Appendix 1 during the surveys, species and their vocalizing individuals recorded will be enumerated and recorded according to the habitat(s) they are utilising.

#### 3.3 HERPETOFAUNA SURVEY

3.3.1 Reptile and amphibian surveys will be conducted along transects shown in Appendix 1 during surveys careful searches of appropriate microhabitats and refugia for reptiles and their vocalizing individuals will be undertaken and all reptiles observed will be identified and counted.

#### 3.4 DRAGONFLY SURVEY

3.4.1 Dragonfly surveys will be conducted along transects shown in Appendix 1 during surveys all dragonflies seen will be identified and counted as accurately as possible.

### **3.5 BUTTERFLY SURVEY**

- 3.5.1 Butterfly surveys will be conducted along transects shown in Appendix 1 during surveys all butterflies seen will be identified and counted as accurately as possible.

### **3.6 AQUATIC FAUNA SURVEY**

- 3.6.1 Freshwater fishes and macro-invertebrates will be recorded by direct observation. All species trapped/recorded will be enumerated and identified (to the lowest taxonomic level possible), and the species of conservation importance photographed.

## 4 RESULT

This monitoring survey started on 11<sup>th</sup> February 2023, a rainy day. The day and night survey covered wetland and non-wetland areas. The survey was conducted by transect and at fixed points. All species seen would be identified and counted as accurately as possible.

- Mammal

There was no mammal species recorded in the monitoring area.

- Bird

There were a total of 27 birds individuals from 8 species recorded in the monitoring area. No Golden-headed Cisticola was observed during the bird survey.

- Herpetofauna

There was no reptile species recorded in the monitoring area.  
There was no amphibian species recorded in the monitoring area.

- Butterfly

There was a total of 4 butterfly individuals from 2 species recorded in the monitoring area.

- Dragonfly

There was no odonate species recorded in the monitoring area.

- Freshwater communities

There was no freshwater community recorded in the monitoring area.

**Picture 1**  
Inside the monitoring site



**Picture 2**  
*Phoenicurus aureus* 北紅尾鵯 Daurian Redstart



**Table 4 Result of mammal in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				Non-wetland		Wetland		
				UG	WL	MA	WW	WC
N/A								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 5 Result of Avifauna in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				Non-wetland		Wetland		
				UG	WL	MA	WW	WC
<i>Spilopelia chinensis</i>	Spotted Dove	珠頸斑鳩					2	
<i>Pycnonotus jocosus</i>	Red-whiskered Bulbul	紅耳鶯					7	
<i>Phylloscopus fuscatus</i>	Dusky Warbler	褐柳鶯					2	
<i>Phylloscopus inornatus</i>	Yellow-browed Warbler	黃眉柳鶯		2				
<i>Prinia flaviventris</i>	Yellow-bellied Prinia	黃腹鷦鶯		1			2	
<i>Orthotomus sutorius</i>	Common Tailorbird	長尾縫葉鶯		3				
<i>Garrulax perspicillatus</i>	Masked Laughingthrush	黑臉噪鶯					7	
<i>Phoenicurus aureus</i>	Daurian Redstart	北紅尾鶯					1	

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 6 Result of reptile in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				Non-wetland		Wetland		
				UG	WL	MA	WW	WC
N/A								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse



**Table 7 Result of amphibian in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				Non-wetland		Wetland		
				UG	WL	MA	WW	WC
N/A								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse  
 + Species appeared but uncountable

**Table 8 Result of butterfly in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				Non-wetland		Wetland		
				UG	WL	MA	WW	WC
<i>Mycalesis mineus</i>	Dark Brand Bush Brown	小眉眼蝶				2		
<i>Abisara echerius</i>	Plum Judy	蛇目褐蛱蝶		2				

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 9 Result of Odonate in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				Non-wetland		Wetland		
				UG	WL	MA	WW	WC
N/A								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 10 Result of freshwater communities in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				Non-wetland		Wetland		
				UG	WL	MA	WW	WC
N/A								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

## 5 DISCUSSION

Data analysis was carried out to compare with the biodiversity within the site boundary in the same month over years. General description of the ecological conditions is first revealed in terms of abundance as well as species richness, following by statistical analysis of the existing database. The result is considered as significant whenever the drop of diversity indexes exceeds the percentages mentioned in previous sections 2.2 and 2.3.

5.1 Total abundance and species richness in February over years were compared to show the trends. Figures 1 and 2 indicate the total species richness and total abundance within the site boundary respectively.

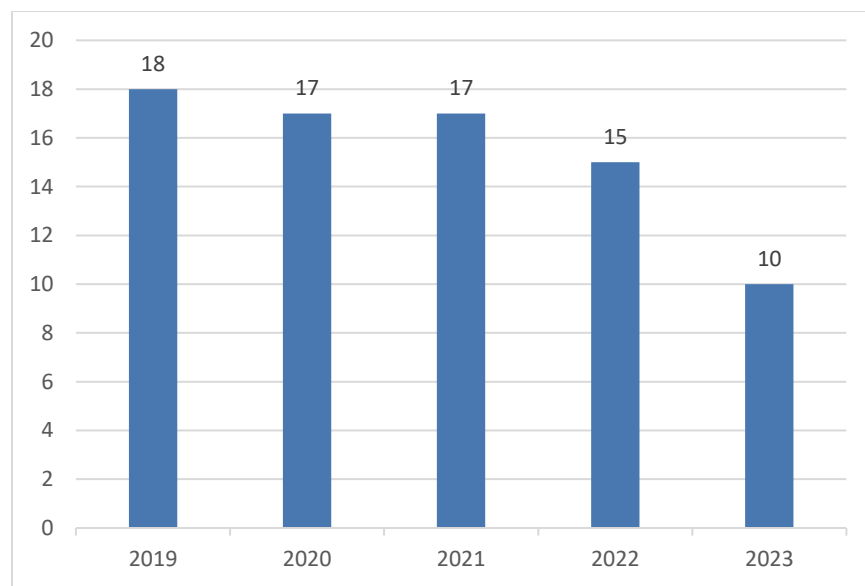


Figure 1: Bar chart showing the total species richness within site boundary from 2019 to 2023 (Actual quantity annotated at the top of each bar)

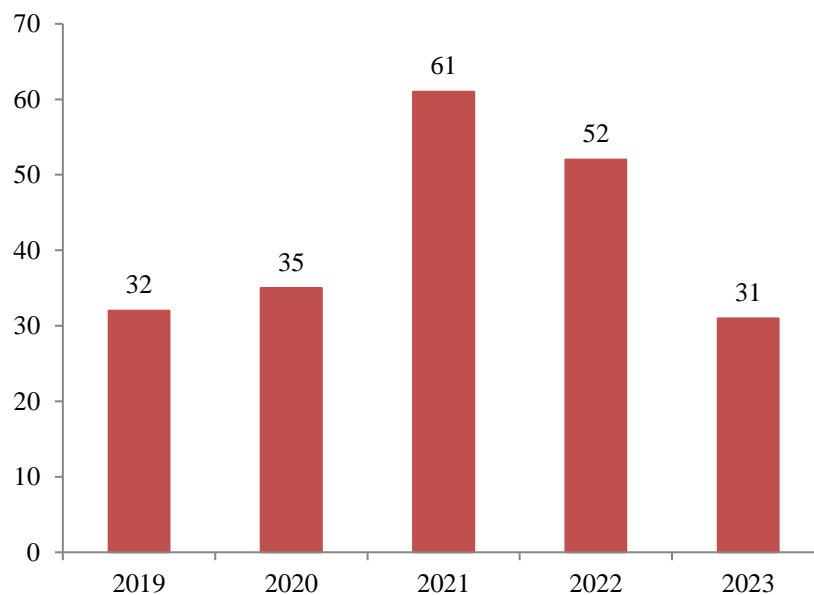


Figure 2: Bar chart showing the total abundance within site boundary from 2019 to 2023 (Actual quantity annotated at the top of each bar)

5.2 As results in section 4 were categorized by taxa, a detailed breakdown of each taxon is shown in figure 3 to further investigate the trend of specific taxa over contract period.

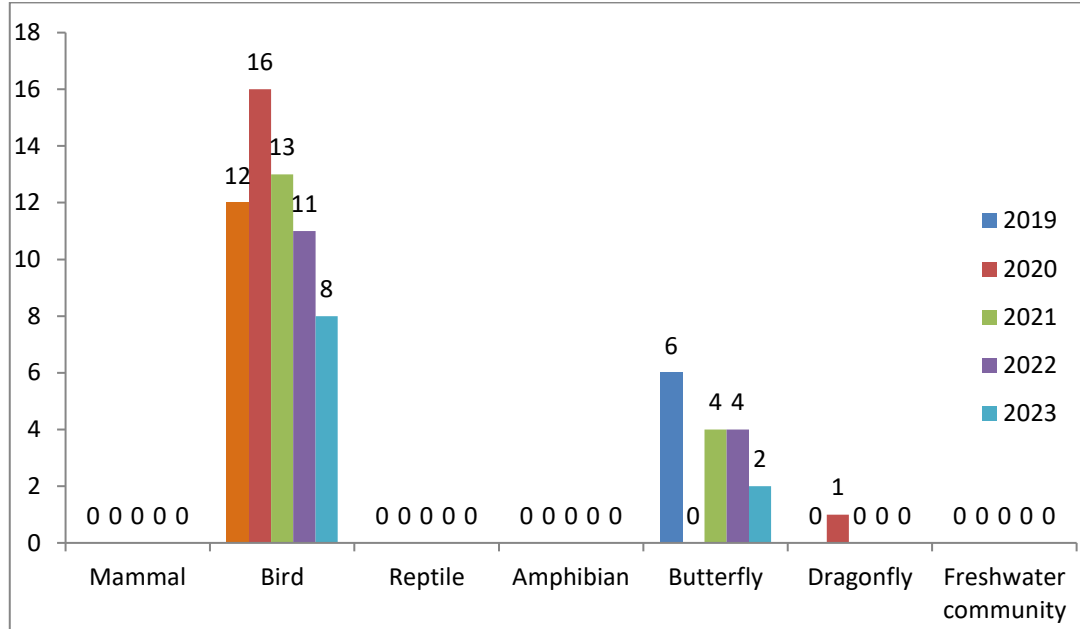


Figure 3: Bar chart showing the species richness within site boundary by taxa from 2019 to 2023 (Actual quantity annotated at the top of each bar)

5.3 According to EM&A Manual, monitoring measures was determined by the species diversity of types of sensitive habitats, i.e. non-wetland and wetland habitats. Abundance and species richness by habitat type in February over years were compared in Figures 4 and 5.

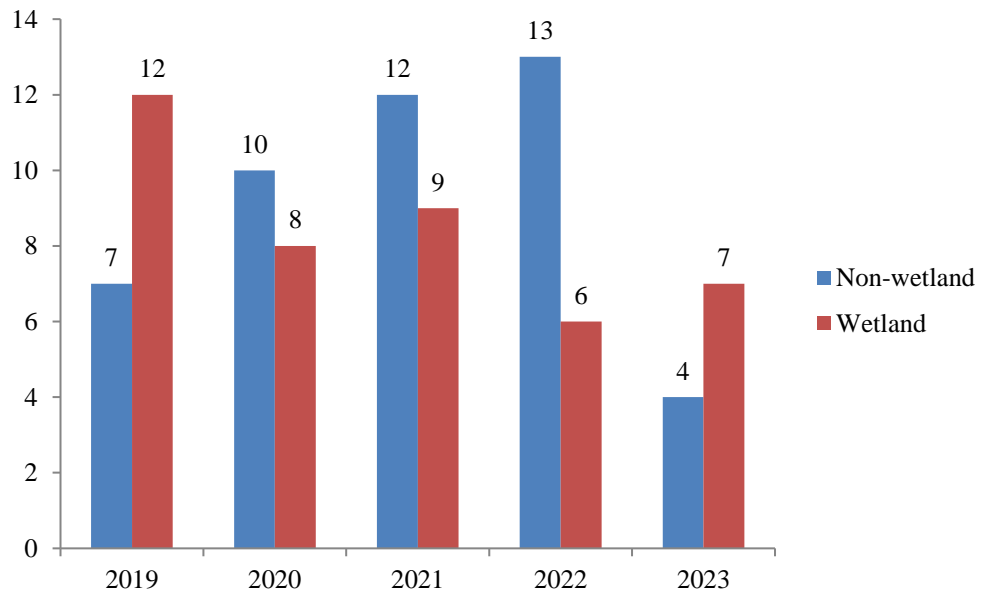


Figure 4: Bar chart showing the species richness based on habitat type from 2019 to 2023 (Actual quantity annotated at the top of each bar)


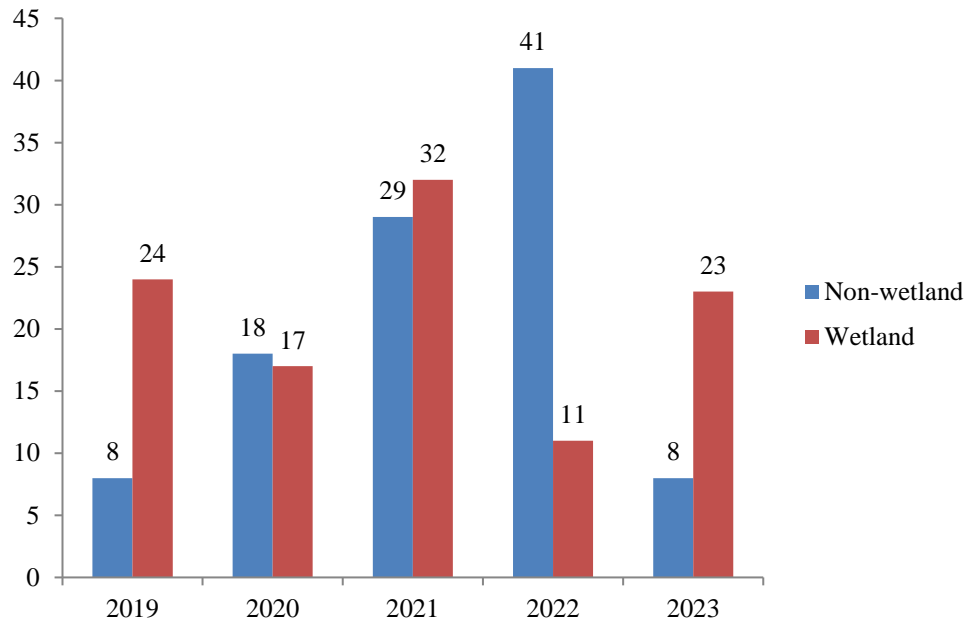


Figure 5: Bar chart showing the abundance based on habitat type from 2019 to 2023  
(Actual quantity annotated at the top of each bar)

5.4 After analysing survey results in February from 2019 to 2023, there was no significant drop in species richness and abundance for wetland habitat. Yet, good site practice during construction, with reference to EM&A Manual, is required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. In addition, implementing proper waste disposal is necessary to reduce contamination to water and soil. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.




## **Appendix I – Transect Routes for Contract CV/2016/10**

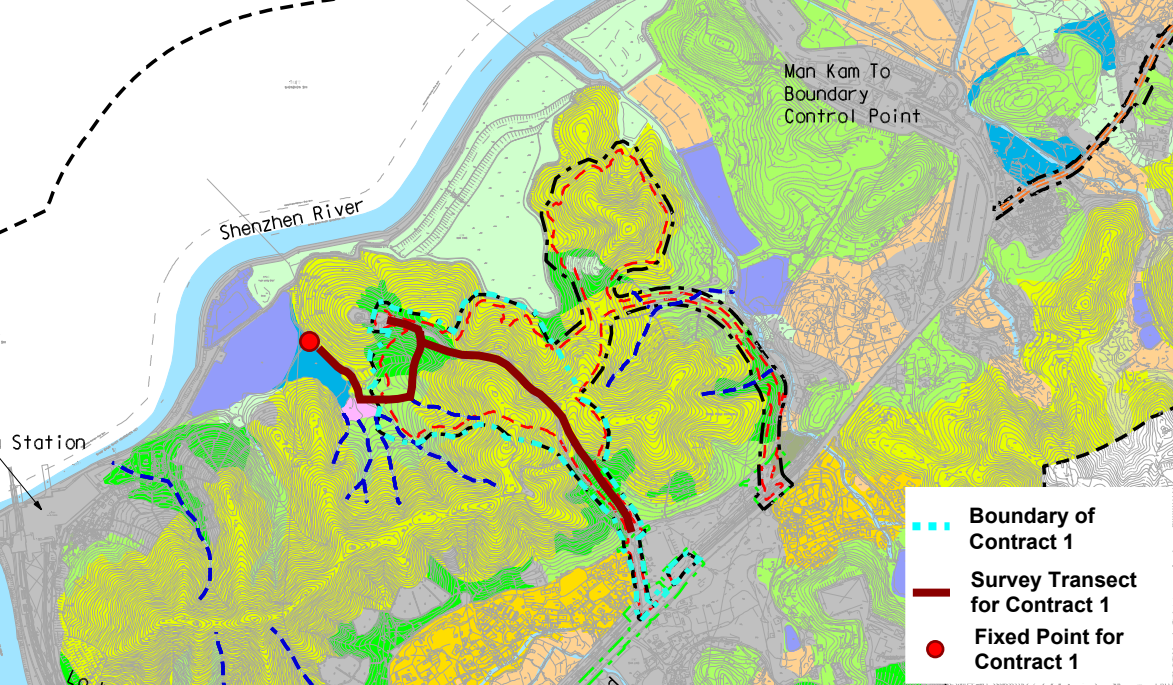

Shenzhen River

Man Kam To  
Boundary  
Control Point

Station

-  Boundary of Contract 1
-  Survey Transect for Contract 1
-  Fixed Point for Contract 1


**Ecological Survey Report for  
Contract CV/2017/02**

## **Contract No. CV/2017/02**

### **Development of Columbarium at Sandy Ridge Cemetery – Infrastructural Works at Man Kam To Road and Lin Ma Hang Road**

---

## **Monthly Report of Ecologically Sensitive Habitats Monitoring – February 2023**

Revision	0	
Date of issue	1 March 2023	
Prepared by	Alan Lam	
Reviewed by	Rachel Siu	
Verified by	Mike Leung	



## Table of Contents

<b>1</b>	<b>INTRODUCTION</b>	<b>4</b>
1.1	BACKGROUND	4
1.2	OBJECTIVE	4
<b>2</b>	<b>ECOLOGICALLY SENSITIVE HABITATS</b>	<b>5</b>
2.1	DESCRIPTION OF HABITATS	5
2.2	MONITORING MEASURES OF WETLAND HABITATS	6
2.3	MONITORING MEASURES OF NON-WETLAND HABITATS	6
<b>3</b>	<b>METHODOLOGY</b>	<b>7</b>
3.1	MAMMAL SURVEY	7
3.2	BIRD SURVEY	7
3.3	HERPETOFAUNA SURVEY	7
3.4	DRAGONFLY SURVEY	7
3.5	BUTTERFLY SURVEY	8
3.6	AQUATIC FAUNA SURVEY	8
<b>4</b>	<b>RESULT</b>	<b>9</b>
<b>5</b>	<b>DISCUSSION</b>	<b>13</b>
	<b>Appendix I – Transect Routes for Contract CV/2017/02</b>	<b>16</b>

<b><u>LIST OF TABLE</u></b>	
Table 1	Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna
Table 2	Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna
Table 3	Survey Schedule
Table 4	Result of mammal in survey
Table 5	Result of Avifauna in survey
Table 6	Result of reptile in survey
Table 7	Result of amphibian in survey
Table 8	Result of butterfly in survey
Table 9	Result of Odonate in survey
Table 10	Result of freshwater communities in survey

<b><u>LIST OF APPENDIX</u></b>	
Appendix I	Transect Routes for Contract CV/2017/02

<b><u>LIST OF FIGURES</u></b>	
Figure 1	Bar chart showing the total species richness within site boundary from 2019 to 2023
Figure 2	Bar chart showing the total abundance within site boundary from 2019 to 2023
Figure 3	Bar chart showing the species richness within site boundary by taxa from 2019 to 2023
Figure 4	Bar chart showing the species richness based on habitat type from 2019 to 2023
Figure 5	Bar chart showing the abundance based on habitat type from 2019 to 2023

# 1 INTRODUCTION

## 1.1 BACKGROUND

- 1.1.1 The main objective of the proposed site formation and associated infrastructural works for development of columbarium, crematorium (C&C) and related facilities at Sandy Ridge Cemetery is to increase the public cremation services and supply of public niches to meet the future demand.
- 1.1.2 The project includes site formation and associated works for development of C&C facilities at the Sandy Ridge Cemetery, road works within Sandy Ridge Cemetery, widening a section of Lin Ma Hang Road (from 6.5m to 7.3m), provision of off-site pick-up/drop-off points for shuttle buses as well as barging point at Siu Lam, Lok On Pai.
- 1.1.3 The Environmental Impact Assessment (EIA) report, including Environmental Monitoring and Audit Manual (EM&A Manual), was approved with conditions on 8 August 2016 (Register No.: AEIAR-198/2016). EPD issued an Environmental Permit (EP) for the Project (EP-534/2017) on 7 April 2017, variation of EP (EP-534/2017/A) were issued on 24 December 2018.
- 1.1.4 According to Clause 3.1 of the EP (EP-534/2017/A), “The Permit Holder shall implement the EM&A programme in accordance with the procedures and requirements as set out in the EM&A Manual. Any changes to the programme shall be justified by the ET Leader and verified by the IEC as conforming to the information and requirements contained in the EM&A Manual before submission to the Director for approval”.
- 1.1.5 This Ecologically Sensitive Habitats Monitoring Methodology articulates the protocol of monitoring the ecology of concerned habitats as specified in EM&A Manual.

## 1.2 OBJECTIVE

- 1.2.1 According to approved EIA report (AEIAR-198/2016), habitat types within project boundary comprise of watercourse, grassland, upland grassland, plantation, woodland and developed area. Natural habitats were of moderate ecological value in terms of species diversity, species rarity, species abundance, ecological linkage as well as nursery. Moreover, 0.3ha of wet woodland on the northern side of Sandy Ridge was deemed habitat with high ecological value. Four types of habitats were regarded as ecologically sensitive habitats, namely wet woodland, watercourses, upland grassland and woodland. Considering human disturbance in upcoming construction and operation phases, ecologically sensitive habitats shall be monitored in accordance with EM&A Manual.
- 1.2.2 The objective of ecologically sensitive habitats monitoring is to evaluate the effectiveness of measures to minimize impacts on concerned habitats from disturbance and pollution.

## 2 ECOLOGICALLY SENSITIVE HABITATS

### 2.1 DESCRIPTION OF HABITATS

- 2.1.1 In order to monitor the effectiveness of the measures to the minimise impact on ecologically sensitive habitats from disturbance and pollution, monthly monitoring during construction and operation phases is required as specified in EM&A Manual. Standard faunal transect and sampling surveys cover both wetland and non-wetland habitats:

Wetland habitats	Non-wetland habitats
Wet Woodland Watercourses	Upland Grassland Woodland

- 2.1.2 Wet woodland is small patch present on northwest of the project boundary, and is confined by the marsh area to the north and the secondary woodland to the east, south and south-west parts. A number of mature trees *Cleistocalyx nervosum* and *Acronychia pedunculata* form the tree canopy, with other self-sown shrubs (including *Psychotria asiatica*, *Ligustrum sinense* and *Glochidion lanceolarium*) and trees (*Aporosa dioica* and *Litsea monopetala*). Whilst botanically it comprises of naturally regenerated secondary woodland and ground level are a series of small braided streams and weep points which even during the dry season remain wet. This creates a rather uncommon habitat in Hong Kong offering suitable conditions for a good assemblage of common wetland species. The wet woodland provides a good assemblage of micro-habitats, which is relatively undisturbed and has good linkages to other natural habitats. Several species of conservation importance were recorded in EIA report from this habitat: East Asian Porcupine, Leopard Cat, Red Muntjac, Two-striped Grass Frog, Small Snakehead, *Somaniathelphusa zanklon*, Dancing Shadow-emerald.
- 2.1.3 Seasonal watercourse running west to east in the eastern part of the area inside the Project boundary is shallower in gradient than those running off the hillside. This seasonal watercourse is heavily vegetated with wetland-associated herbs including *Commelina diffusa*, *Polygonum chinense*, *Colocasia esculenta* and *Dracaena sandariana*. A mature tree of *Aquilaria sinensis* was recorded at the bank of the seasonal watercourse to the west of the Sandy Ridge Cemetery Office. Seasonal watercourses are restricted to the steeper slopes within the project boundary and are characterised by being entirely dry for much of the dry season. However, endemic crab *S. zanklon* population is supported by ephemeral watercourses close to the project boundary.
- 2.1.4 Upland grassland is the major habitat within the project boundary. The semi-natural habitat is dominated by typical upland grassland species: fern *Dicranopteris pedata*, grass *Neyraudia reynaudiana*, *Miscanthus floridulus*, climbing vines *Smilax china*, *Smilax glabra*, and shrubs such as *Rhodomyrtus tomentosa*, *Breynia fruticosa* and *Helicteres angustifolia*. Approximately 30 flowering spikes of two orchid species Bamboo Orchid and Toothed Habenaria were recorded near the hill top in the northern part of this upland grassland. Golden-headed Cisticola, which is considered as Local Concern by Fellowes *et al.* (2002), was also recorded in upland grassland on Sandy Ridge, including a proved breeding record of fledged young in September 2013. In addition, numerous species of conservation interest were recorded in EIA report, such as East Asian Porcupine, Leopard Cat, Red Muntjac, Great Swift, Tamil Grass Dart, Small Three-ring and Small Grass Yellow.

2.1.5 Scattered patches of woodland are present throughout the assessment area, with the largest contiguous block located immediately to the east of the project boundary. These woodlands are relatively young with single-layered of canopy dominants (~10 – 15m tall) including *A. dioica*, *Bridelia tomentosa*, *Cinnamomum burmannii*, *Daphniphyllum calycinum*, *Litsea glutinosa*, *Rhus succedanea*, and *Zanthoxylum avicennae*. Such areas comprise secondary woodland which is largely derived from natural regeneration and colonisation of trees as a result of seed dispersal by birds and/or bats. A mature tree of *A. sinensis* is located at the woodland edge at the central part of the Project according to EIA report.

## 2.2 MONITORING MEASURES OF WETLAND HABITATS

2.2.1 Wetland habitats include wet woodland and watercourses. Monitoring surveys using standardised quantitative methodology will be conducted at fixed points. For seasonal watercourse, survey shall be conducted whenever the habitat appears.

2.2.2 Measures to respond to decreases in numbers of aquatic fauna using the wetland habitats and action and limit levels to trigger these measures are detailed in Table 1.

Action Level	Response	Limit Level	Response
Reduction in taxa diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in taxa diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

Table 1 Action and Limit Levels and Responses to Evidence of Declines in Aquatic Fauna

## 2.3 MONITORING MEASURES OF NON-WETLAND HABITATS

2.3.1 Non-wetland habitats consist of upland grassland and woodland. Monthly quantitative surveys of non-aquatic fauna will be conducted using standard route transect counts.

2.3.2 Measures to respond to decreases in numbers of non-aquatic fauna using the non-wetland habitats and action and limit levels to trigger these measures are detailed in Table 2.

Action Level	Response	Limit Level	Response
Reduction in species diversity by 30%	Investigate cause and if cause identified as related to the project instigate remedial action to remove or reduce source of disturbance.	Reduction in species diversity by 50%	Investigate cause and if cause identified as related to the project instigate remedial action.

Table 2 Action and Limit Levels and Responses to Evidence of Declines in Non-Aquatic Fauna

### 3 METHODOLOGY

The ecological survey includes all taxa being investigated in EIA report. Table 3 summarizes schedule of faunal surveys.

Month	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Mammals	√	√	√	√	√	√	√	√	√	√	√	√
Birds (day)	√	√	√	√	√	√	√	√	√	√	√	√
Birds (night)				√	√	√	√	√	√	√		
Herpetofauna				√	√	√	√	√	√	√		
Dragonflies			√	√	√	√	√	√	√	√		
Butterflies			√	√	√	√	√	√	√	√		
Aquatic fauna	√	√	√	√	√	√	√	√	√	√	√	√

Table 3 Survey Schedule

#### 3.1 MAMMAL SURVEY

3.1.1 Mammal surveys will be conducted along the transects shown in Appendix 1 during both daytime and night time periods. Along with direct observations, other field signs, such as scats and tracks, will be searched and recorded if present.

#### 3.2 BIRD SURVEY

3.2.1 Bird surveys will be conducted along the transects shown in Appendix 1 during the surveys, species and their vocalizing individuals recorded will be enumerated and recorded according to the habitat(s) they are utilising.

#### 3.3 HERPETOFAUNA SURVEY

3.3.1 Reptile and amphibian surveys will be conducted along transects shown in Appendix 1 during surveys careful searches of appropriate microhabitats and refugia for reptiles and their vocalizing individuals will be undertaken and all reptiles observed will be identified and counted.

#### 3.4 DRAGONFLY SURVEY

3.4.1 Dragonfly surveys will be conducted along transects shown in Appendix 1 during surveys all dragonflies seen will be identified and counted as accurately as possible.

### **3.5 BUTTERFLY SURVEY**

- 3.5.1 Butterfly surveys will be conducted along transects shown in Appendix 1 during surveys all butterflies seen will be identified and counted as accurately as possible.

### **3.6 AQUATIC FAUNA SURVEY**

- 3.6.1 Freshwater fishes and macro-invertebrates will be recorded by direct observation. All species trapped/recorded will be enumerated and identified (to the lowest taxonomic level possible), and the species of conservation importance photographed.

## 4 RESULT

This monitoring survey started on 11<sup>th</sup> February 2023, a rainy day. The day and night survey covered wetland and non-wetland areas. The survey was conducted by transect and at fixed point. All species seen would be identified and counted as accurately as possible.

- **Mammal**  
There was no mammal recorded in the monitoring area.
- **Bird**  
There were total of 4 bird individuals from 3 species recorded in the monitoring area. No Golden-headed Cisticola was observed during the bird survey.
- **Herpetofauna**  
There was no reptile recorded in the monitoring area.  
There was no amphibian recorded in the monitoring area.
- **Butterfly**  
There was no butterfly recorded in the monitoring area.
- **Dragonfly**  
There was no odonate recorded in the monitoring area.
- **Freshwater communities**  
There were 2 species of freshwater fish recorded in the monitoring area.



**Picture 1**

Watercourse in monitoring area.



**Picture 2**

Watercourse in monitoring area.



**Table 4 Result of mammal in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				UG	WL	MA	WW	WC
N/A								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 5 Result of Avifauna in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				UG	WL	MA	WW	WC
<i>Amaurornis phoenicurus</i>	White-breasted Waterhen	白胸苦惡鳥				1		
<i>Prinia flaviventris</i>	Yellow-bellied Prinia	黃腹鷓鴣		2				
<i>Orthotomus sutorius</i>	Common Tailorbird	長尾縫葉鶯		1				

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 6 Result of reptile in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				UG	WL	MA	WW	WC
N/A								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 7 Result of amphibian in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				UG	WL	MA	WW	WC
N/A								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse  
 + Species appeared but uncountable

**Table 8 Result of butterfly in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				UG	WL	MA	WW	WC
N/A								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 9 Result of Odonate in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				UG	WL	MA	WW	WC
N/A								

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse

**Table 10 Result of freshwater communities in survey**

Scientific Name	Common Name	Chinese Name	Conservation Status	11/2/2023				
				UG	WL	MA	WW	WC
<i>Gambusia affinis</i>	Mosquito fish	食蚊魚						+
<i>Puntius semifasciolatus</i>	Chinese Barb	五線無鬚鯪						+

\*UG: Upland Grassland | WL: Woodland | MA: Marsh | WW: Wet Woodland | WC: Watercourse  
 + Species appeared but uncountable

## 5 DISCUSSION

Data analysis was carried out to compare with the biodiversity within the site boundary in the same month over years. General description of the ecological conditions is first revealed in terms of abundance as well as species richness, following by statistical analysis of the existing database. The result is considered as significant whenever the drop of diversity indexes exceeds the percentages mentioned in previous sections 2.2 and 2.3.

5.1 Total abundance and species richness in February over years were compared to show the trends. Figures 1 and 2 indicate total species richness and total abundance within the site boundary respectively.

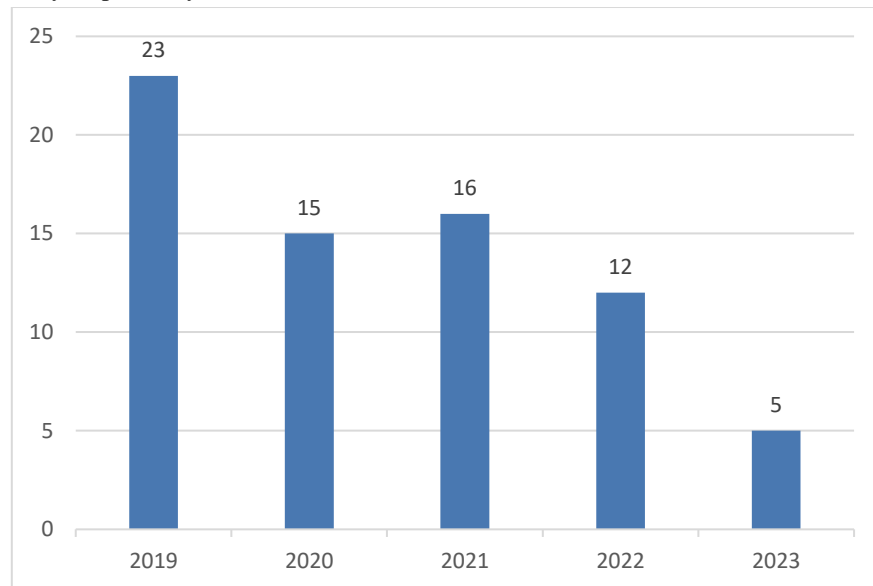


Figure 1: Bar chart showing the total species richness within site boundary from 2019 to 2023 (Actual quantity annotated at the top of each bar)

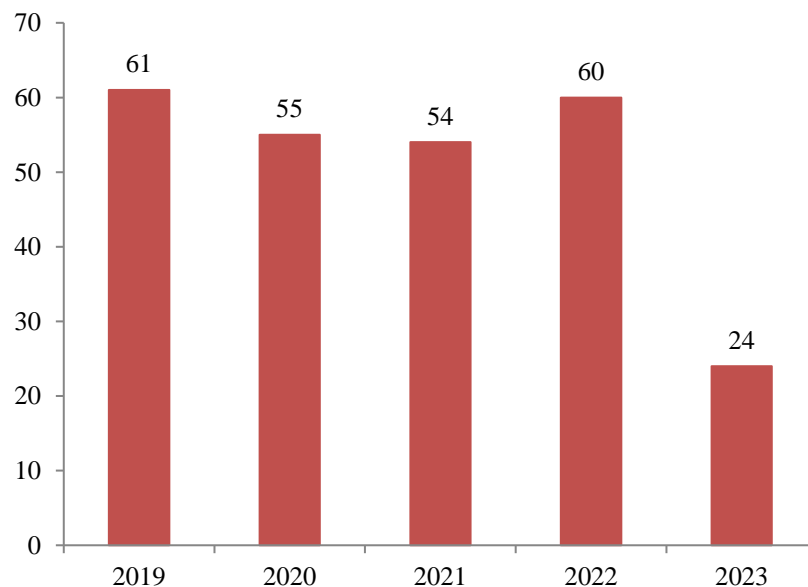


Figure 2: Bar chart showing the total abundance within site boundary from 2019 to 2023 (Actual quantity annotated at the top of each bar)

5.2 As results in section 4 were categorized by taxa, a detailed breakdown of each taxon is shown in figure 3 to further investigate the trend of specific taxa over contract period.

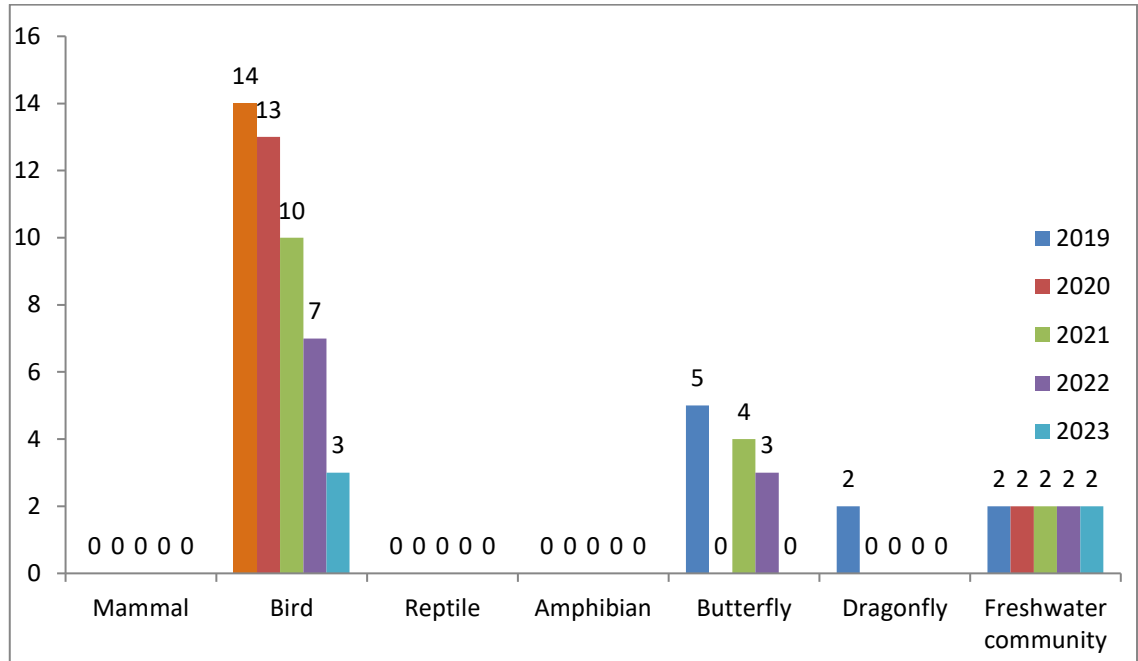


Figure 3: Bar chart showing the species richness within site boundary by taxa from 2019 to 2023 (Actual quantity annotated at the top of each bar)

5.3 According to EM&A Manual, monitoring measures was determined by the species diversity of types of sensitive habitats, i.e. non-wetland and wetland habitats. Abundance and species richness by habitat type in February over years were compared in figures 4 and 5.

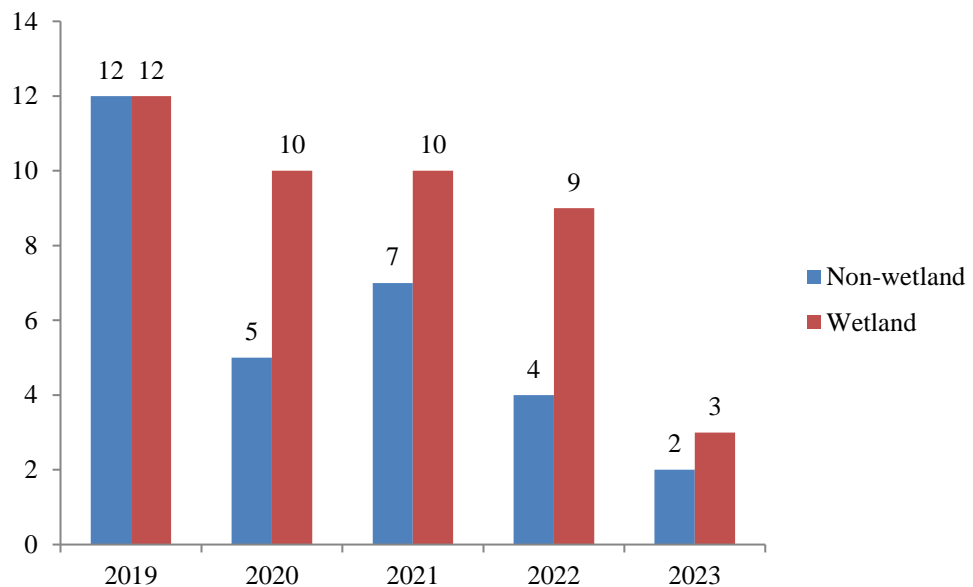


Figure 4: bar chart showing the species richness based on habitat type from 2019 to 2023 (Actual quantity annotated at the top of each bar)


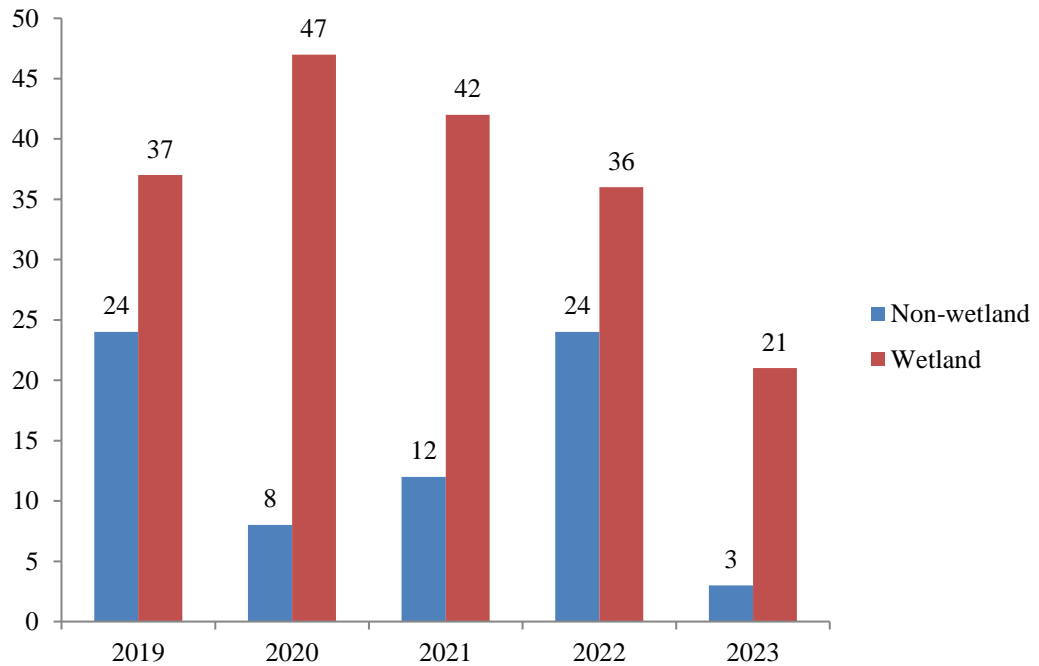


Figure 5: bar chart showing the abundance based on habitat type from 2019 to 2023  
(Actual quantity annotated at the top of each bar)

5.4 After analysing survey results in February from 2019 to 2023, there was a decrease in species richness and abundance for wetland and non-wetland habitats. Still, a good site practice during construction, with reference to EM&A Manual, is required to prevent or alleviate environmental impacts. For instance, the size of work areas should be minimized and disturbed areas should be reinstated immediately after completion of construction works. In addition, implementing proper waste disposal is necessary to reduce contamination to water and soil. Continuous monitoring is also recommended to inspect any significant decrease in species diversity.

## **Appendix I – Transect Routes for Contract CV/2017/02**

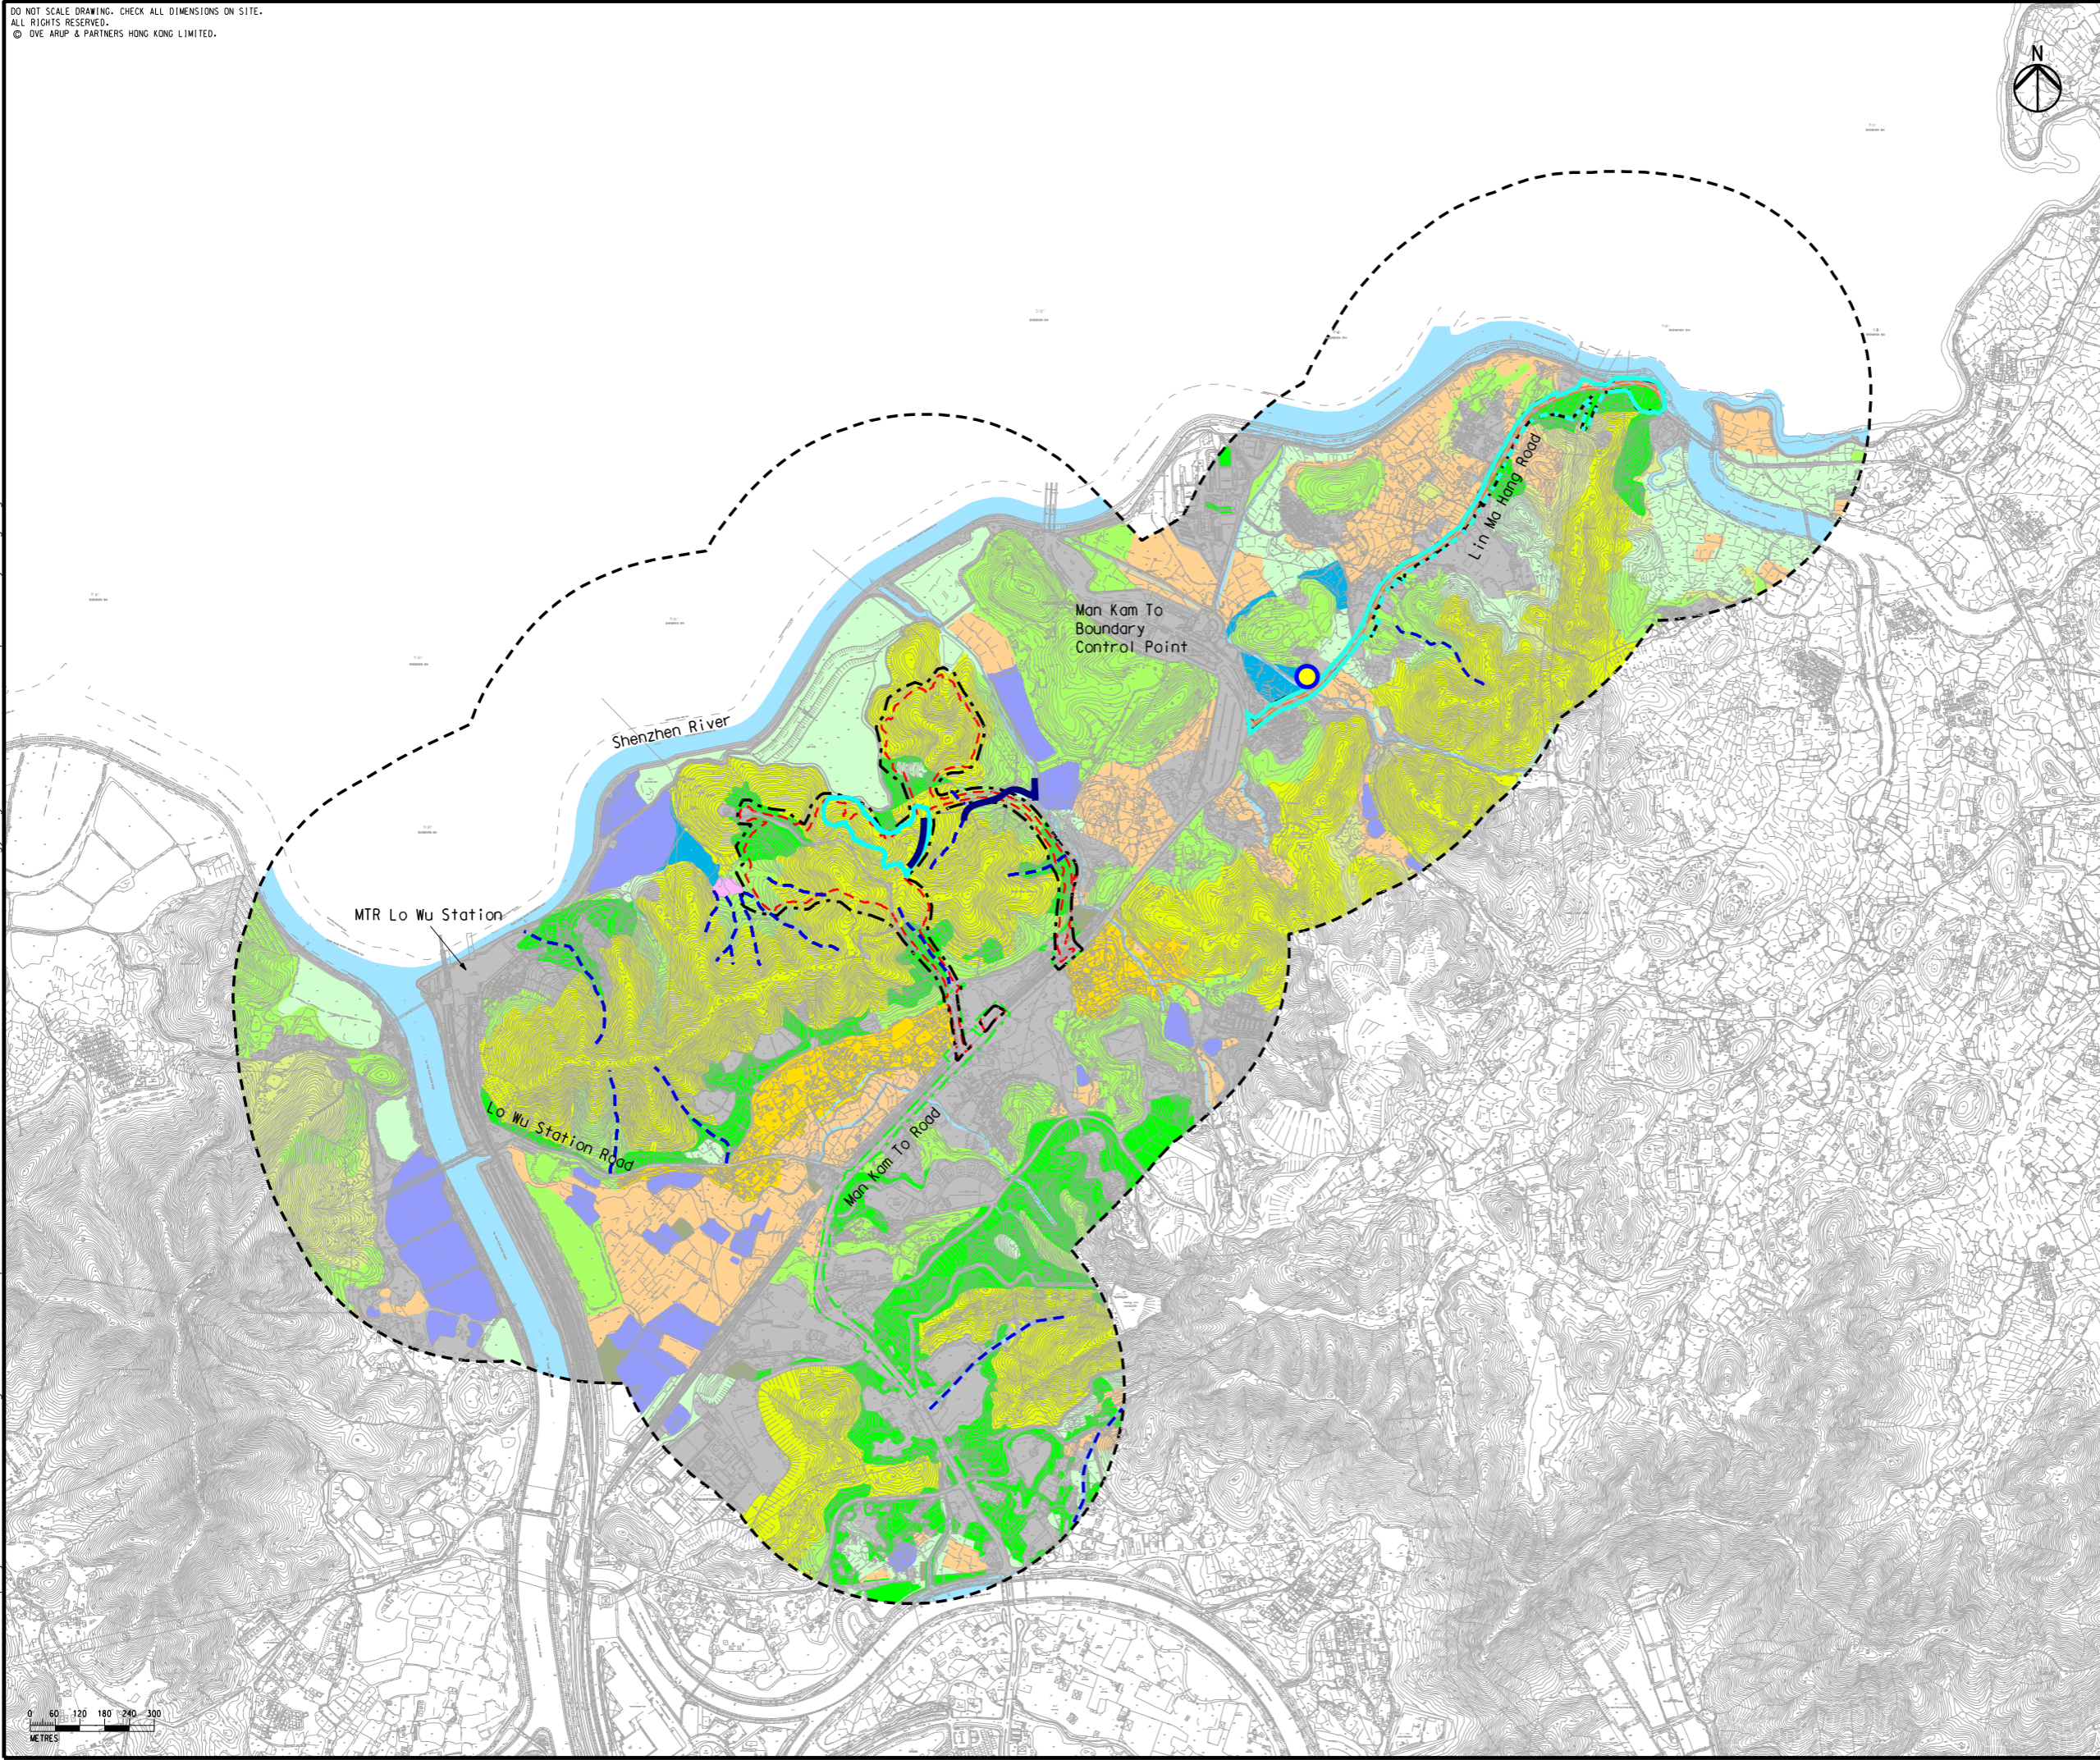

Legend

- Project Boundary
- Utilities Construction
- Sandy Ridge Works Area
- Lin Ma Hang Road Works Area
- 500m Assessment Area
- Watercourse
- Seasonal Watercourse
- Pond
- Developed Area
- Agricultural Land
- Marsh
- Wasteland
- Grassland
- Upland Grassland
- Shrubland
- Plantation
- Woodland
- Wet Woodland
- Village Area
- Site boundary of Contract 2
- Survey Transect for Contract 2
- Fixed Point for Contract 2

G	SEVENTH ISSUE	GL	02/16
F	SIXTH ISSUE	GL	01/16
E	FIFTH ISSUE	GL	12/15
D	FOURTH ISSUE	GL	10/15
Rev	Description	By	Date

Consultant  
**ARUP**

Contract No. and Title:  
 Agreement No. CE 1/2013(CE)  
 Site Formation and Associated  
 Infrastructural Works for Development  
 of Columbarium, Crematorium and  
 Related Facilities at Sandy Ridge  
 Cemetery - Design and Construction


Drawing title  
**Habitat Map at Sandy Ridge**

Drawing no. **Figure 9.4b** Rev. **G**

Drawn GL	Date 02/16	Checked EL	Approved ST
Scale AS SHOWN		Status PRELIMINARY	

COPYRIGHT RESERVED

土木工程拓展署  
Civil Engineering and  
Development Department





## **Appendix L**

### **Landscape & Visual Inspection Checklist**

**Contract No. CV/2016/10**

**Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery**

**Landscape and Visual Impact Assessment Checklist for Site Audit**

**Date/ Time: 28/02/2023 10:30 Weather: Fine/ Overcast/ Rain/ Windy**

Item	Mitigation Measures	Implementation			Actions/ Remarks
		Yes	No	N/A	
<b>1</b>	<b>Landscape and Visual</b>				
1.1	Is the construction period become shortened?			✓	Under review.
1.2	Is the work site confined within site boundaries and without encroaching into the landscape resources offsite?	✓			
1.3	Is the site kept clean and tidy (E.g. storage of materials, location and appearance of site accommodation being well positioned)	✓			
1.4	Is the construction site screened properly by hoardings or noise barriers in visually unobstructed colours?	✓			
1.5	Is the erosion and dust control for exposed soil well performed during excavation work? (E.g. Exposed soil shall be covered or “camouflaged” and watered frequently. Areas that are expected to be left with bare soil for a long period of time should be hydro seeded and / or covered with suitable protective fabrics.)	✓			
1.6	Are the woodland, plantation and other vegetation being protected and preserved in accordance with DEVB TC(W) No. 07/2015(E.g. Set up Tree Protection Zone)?	✓			
1.7	Are the trees which are in direct conflict with the development proposal being transplanted as far as practical in accordance with and DEVB TC(W) No. 07/2015?	✓			
1.8	Are compensatory planting for trees being provided to compensate the trees felled in accordance with DEVB TC(W) No. 07/2015?			✓	Tree planting works have not yet been commenced.
1.9	Are precautionary control measures to protect natural streams and rivers from adverse impact being implemented in accordance with ETWWB TCW No. 5/2005? (E.g. Construction debris and spoil should be covered up and properly disposed)	✓			
1.10	Is light and glare control such as hooding being implemented during construction and operation to minimize light pollution and night time glare? (E.g. All security floodlights for construction sites should be equipped with adjustable shield, frosted diffusers and reflective covers)	✓			

**Summary / Remarks:**

**Follow up actions taken by Contractor for previous comments:**

N/A

**New observation:**

N/A

**Reminders:**

1. Contractor is reminded to set up TPZ of proper size and with appropriate material around retain trees according to approved method statement.
2. Contractor is reminded to prevent the construction material pile within TPZ and ensure no works is allowed within the TPZ.
3. Transplanted trees T2465 and T2928 were in fair health condition with normal foliage color and density. Contractor is reminded to provide proper maintenance according to approved method statement.

**Photo Record:**

**Fig A.**



General view (1)

**Fig B.**



General view (2)

**Fig C.**



General view (3)

**Fig D.**



General view (4)

**Fig E.**



Transplanted tree (T-2465)

**Fig F.**



Transplanted tree (T-2928)

**Contract No. CV/2017/02**

**Site Formation and Associated Infrastructural Works for Development of Columbarium, Crematorium and Related Facilities at Sandy Ridge Cemetery**

**Development of Columbarium at Sandy Ridge Cemetery –**

**Infrastructural Works at Man Kam To Road and Lin Ma Hang Road**

**Landscape and Visual Impact Assessment Checklist for Site Audit**

**Date/ Time: 28/02/2023 11:30 Weather: Fine/ Overcast/ Rain/ Windy**

Item	Mitigation Measures	Implementation			Actions/ Remarks
		Yes	No	N/A	
<b>1</b>	<b>Landscape and Visual</b>				
1.1	Is the construction period become shortened?			✓	Under review
1.2	Is the work site confined within site boundaries and without encroaching into the landscape resources offsite?	✓			
1.3	Is the site kept clean and tidy (E.g. storage of materials, location and appearance of site accommodation being well positioned)	✓			
1.4	Is the construction site screened properly by hoardings or noise barriers in visually unobstructed colours?	✓			
1.5	Is the erosion and dust control for exposed soil well performed during excavation work? (E.g. Exposed soil shall be covered or “camouflaged” and watered frequently. Areas that are expected to be left with bare soil for a long period of time should be hydro seeded and / or covered with suitable protective fabrics.)	✓			
1.6	Are the woodland, plantation and other vegetation being protected and preserved in accordance with DEVB TC(W) No. 07/2015(E.g. Set up Tree Protection Zone)?	✓			
1.7	Are the trees which are in direct conflict with the development proposal being transplanted as far as practical in accordance with and DEVB TC(W) No. 07/2015?			✓	
1.8	Are compensatory planting for trees being provided to compensate the trees felled in accordance with DEVB TC(W) No. 07/2015?			✓	
1.9	Are precautionary control measures to protect natural streams and rivers from adverse impact being implemented in accordance with ETWWB TCW No. 5/2005? (E.g. Construction debris and spoil should be covered up and properly disposed)			✓	
1.10	Is light and glare control such as hooding being implemented during construction and operation to minimize light pollution and night time glare? (E.g. All security floodlights for construction sites should be equipped with adjustable shield, frosted diffusers and reflective covers)			✓	

**Summary / Remarks:**

**Follow up actions taken by Contractor for previous comments:**

N/A

**New Observation:**

N/A

**Reminders:**

1. Contractor is reminded to set up TPZ of proper size and with appropriate material around retain trees according to approved method statement. Contractor should prevent any construction material pile within TPZ and ensure no works is allowed within the TPZ.

**Photo Record:**

**Fig A.**



General view (1)

**Fig B.**



General view (2)

**Fig C.**



General view (3)

**Fig D.**



General view (4)

**Signature:**

		Signature	Date
Recorded by	Registered Landscape Architect		28 Feb 2023
Checked by	Environmental Team Leader		10 Mar 2023
	Independent Environmental Checker		13 March 2023

## **Appendix M**

### **Monthly Summary Waste Flow Table**



## Monthly Summary Waste Flow Table for 2023

Department: Civil Engineering and Development Department      Contract No.: CV/2016/10  
 Contract Title: Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery  
 Commencement Date: 15-Dec-2017      Estimated completion Date 22-Dec-2023      Estimated Contract Sum: 780M

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )
Jan	0.340	0.000	0.000	0.000	0.340	0.000	0.000	0.000	0.000	0.000	0.020
Feb	0.300	0.000	0.000	0.000	0.300	0.000	0.000	0.000	0.000	0.000	0.015
Mar											
Apr											
May											
June											
<b>Sub-total</b>	<b>0.640</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.640</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.035</b>
July											
Aug											
Sept											
Oct											
Nov											
Dec											
<b>Total</b>	<b>0.640</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.640</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.000</b>	<b>0.035</b>

- Notes:
- (1) The waste flow table should cover the whole construction period of the Contract.
  - (2) The original estimates of the C&D materials should be the estimates at contract commencement and should not be altered during construction.
  - (3) Inert C&D materials that are specified in the Contract to be imported for use at the Site shall be separately indicated.
  - (4) The yearly estimates of the C&D materials should be updated as appropriate taking into account the latest works programme etc.
  - (5) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
  - (6) Broken concrete for recycling into aggregates.

## **Appendix N**

### **Complaint Log**

### Complaint Log for Contract 1

Log ref.	Date of complaint	Complaint route	Reference no.	Complaint nature	Investigation fining	Status
1	15-Apr-21	EPD	EPD Ref.: EP3/N07/RN/8770-21	Air Quality	Non-project related	Interim IR was submitted to EPD on 22 April 2021 and included in EM&A Report – Apr 2021
2	11-Feb-22	EPD	EPD Ref.: EP3/N07/RN/03921-22	Noise	Non-project related	Interim IR was submitted to EPD on 25 Feb 2022 and included in EM&A Report – Feb 2021

### Complaint Log for Contract 2

Log ref.	Date of complaint	Complaint route	Reference no.	Complaint nature	Investigation fining	Status
1	4-Sep-20	EPD	EPD Ref.: EP/RN/419300	Water quality	Non-project related	Interim IR was submitted to EPD on 14 Sep 2020 and included in EM&A Report – Sep 2020
2	15-Apr-21	EPD	EPD Ref.: EP3/N07/RN/8770-21	Air Quality	Non-project related	Interim IR was submitted to EPD on 22 April 2021 and Included in EM&A Report – Apr 2020
3	11-Feb-22	EPD	EPD Ref.: EP3/N07/RN/03921-22	Noise	Non-project related	Interim IR was submitted to EPD on 25 Feb 2022 and included in EM&A Report – Feb 2021
4	14-July-22	EPD	EPD Ref.: N07/RN/00014141-22	Soil/muddy water	Non-project related	Interim IR was submitted to EPD on 19 Aug 2022 and included in EM&A Report – Aug 2022
5	23-9-22	EPD	EPD Ref.: N07/RN/00020415-22	Air Quality	Non-project related	Interim IR was submitted to EPD on 30 Sep 2022 and included in EM&A Report – Sep 2022

Name of Department: CEDD

## Monthly Summary Waste Flow Table for 2023

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in Litre)	(in '000kg)
JAN	191.800	0.000	0.000	0.000	191.8	0.000	0.000	0.000	0.000	0.000	5.800
FEB	356.600	0.000	0.000	0.000	356.6	0.000	0.000	0.000	0.000	0.000	9.600
MAR											
APRIL											
MAY											
JUN											
Sub Total	548.400	0.000	0.000	0.000	548.400	0.000	0.000	0.000	0.000	0.000	15.400
JUL											
AUG											
SEP											
OCT											
NOV											
DEC											
Total	548.400	0.000	0.000	0.000	548.400	0.000	0.000	0.000	0.000	0.000	15.400

Notes: \* estimated quantity (pending from EPD NENT (soil) to update the actual quantity)

**Name of Department: CEDD**

Forecast of Total Quantities of C&D Materials to be Generated from the Contract (see Note 4)										
Total Quantity Generated	Hard Rocks and Large Broken Concrete	Reused in the Contract	Reused in Other Projects	Disposed as Public Fill	Imported Fill	Metal	Paper / cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )
0	0	0	0	0	0	0	0	0	1	0

Notes:

- (1) The performance targets are given in PS clause 6(14) above.
- (2) The waste flow table shall also include C&D materials that are specified in the Contractor to be imported for use at the Site.
- (3) Plastic refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- (4) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature
  - Hard Rocks and Large Broken Concrete = Cannot be defined at this stage
  - Imported Fill = Estimated by the Contractor
  - Metal = Estimated by the Contractor
  - Paper/cardboard packaging = Estimated by the Contractor
  - Plastics = Estimated by the Contractor
  - Chemical Waste = Estimated by the Contractor (Spent lubricating oil, assume density 0.9kg/L)
  - Other, e.g. general refuse = Estimated by the Contractor

## **Appendix O**

### **Implementation Schedule for Environmental Mitigation Measures**







EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
		activities.					
S5.5.5.5	Adopt quiet plants during the construction of viaduct, widening of Sha Ling Road, construction of platform for crematorium and widening of Lin Ma Hang Road. The quiet plants should be made reference to the PME listed in the TM or the QPME/ other commonly used PME listed in EPD web pages or taken from BS5228: Part 1: 2009 Noise Control on Construction and Open Sites as far as possible.	Reduce the noise levels of plant items	Contractor	Works area for construction of viaduct, widening of Sha Ling Road, construction of platform for crematorium and widening of Lin Ma Hang Road	Construction phase	<ul style="list-style-type: none"> <li>Annex 5, TM-EIAO</li> </ul>	Implemented * Quiet plants were in used.
S5.5.5.6	Install temporary noise barriers (in the form of site hoardings, approx. 2.4m high) located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening.	Contractor	All construction sites where practicable	Construction phase	Annex 5, TM-EIAO	Implemented where necessary. * Temporary noise barriers are not practicable due to site constraint.
S5.5.5.7	Install movable noise barriers (typical design is wooden framed barrier with a small-cantilevered upper portion of superficial density no less than 7kg/m2 on a skid footing with 25mm thick internal sound absorptive lining), acoustic mat or full enclosure, screen the noisy plants including air compressors, generators etc.	Screen the noisy plant items to be used at all construction sites	Contractor	All construction sites where practicable	Construction phase	Annex 5, TM-EIAO	Implemented where necessary. * Movable noise barriers are not practicable due to site constraint.
S5.5.5.13	Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction noise	Contractor	All construction sites where practicable	Construction phase	Annex 5, TM-EIAO	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S13.2.1.1	Implement a noise monitoring under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected representative noise monitoring station	Construction phase	TM-EIAO	Implemented. * 4 noise monitoring stations were Implemented.
S13.4.1.2							
<b>Operational Noise (Road Traffic Noise)</b>							
S5.6.6.4	<p>Provide a series of noise mitigation measures including absorptive noise barriers and low noise road surfacing materials along Lin Ma Hang Road and Sha Ling Road before operation of the proposed project for existing and planned representative NSRs. Locations of noise mitigation measures are stated as following:</p> <p><i>For existing representative NSRs</i></p> <ul style="list-style-type: none"> <li>• Approx. 12m of absorptive noise barrier 2.5m above road level along Sha Ling Road (MM1);</li> <li>• Approx. 92m of absorptive noise barrier 2.5m above road level along Sha Ling Road (MM2);</li> <li>• Approx. 28m of absorptive noise barrier 3m above road level along Project Road near Sha Ling Road (MM3);</li> <li>• Approx. 51m of absorptive noise barrier 3m above road level along Project Road near Sha Ling Road (MM4);</li> <li>• Approx. 25m of absorptive noise barrier 4m above road level along Lin Ma Hang Road near San Uk Ling (MM5);</li> <li>• Approx. 21m of absorptive noise barrier 4m above road level along Lin Ma Hang Road near San Uk Ling (MM6);</li> <li>• Approx. 14m of absorptive noise barrier 4m above road level along Lin Ma Hang Road near San Uk Ling (MM7);</li> <li>• Approx. 18m of absorptive noise barrier 3m above road level along Lin Ma Hang Road near San Uk Ling (MM8);</li> <li>• Approx. 42m of absorptive noise barrier 3m above road level along temporary pullover space opposite San Uk Ling (MM9);</li> <li>• Approx. 93m of absorptive noise barrier 3m above road level along Lin Ma Hang Road opposite San Uk Ling (MM10);</li> <li>• Approx. 185m of low noise surfacing materials along Lin Ma Hang Road near San Uk Ling (MM11);</li> <li>• For planned representative NSRs</li> <li>• Approx. 36m of absorptive noise barrier 5m above road level along Lin Ma Hang Road near Muk Wu Nga Yiu (MM12);</li> <li>• Approx. 47m of absorptive noise barrier 5m above road level along Lin Ma Hang</li> </ul>	Reduce operation noise from road traffic	Contractor	Refer to Figures 5.6.9 - 5.6.13 of the EIA Report	Prior to operation of the Project for existing representative NSRs. While for barriers to protect planned representative NSRs, it should be constructed before intake of planned representative NSRs.	<ul style="list-style-type: none"> <li>• TM-EIAO</li> </ul>	Shall be implemented Prior to operation of the Project.

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
	<ul style="list-style-type: none"> <li>Road near Muk Wu Nga Yiu (MM13);</li> <li>Approx. 3.1m of absorptive noise barrier 5m above road level along Lin Ma Hang</li> <li>Road near Muk Wu Nga Yiu (MM14);</li> <li>Approx. 3.1m of absorptive noise barrier 5m above road level along Lin Ma Hang</li> <li>Road near Muk Wu Nga Yiu (MM15);</li> <li>Approx. 4.1m of absorptive noise barrier 5m above road level along Lin Ma Hang</li> <li>Road near Muk Wu Nga Yiu (MM16);</li> <li>Approx. 340m of low noise surfacing materials along Lin Ma Hang Road near Muk Wu Nga Yiu (MM17).</li> </ul>						
<b>Water Quality (Construction Phase)</b>							
S6.4.4.1	In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), construction phase mitigation measures shall include the following:	To minimise water quality impact from construction site runoff and general construction activities	Contractor	All construction sites where applicable	Construction phase	<ul style="list-style-type: none"> <li>Water Pollution Control Ordinance</li> <li>ProPECC PN1/94</li> <li>TM-EIAO</li> <li>TM-DSS</li> </ul>	Implemented
S6.4.4.3	<p><u>General Site Operation</u></p> <ul style="list-style-type: none"> <li>At the start of site establishment, perimeter cut-off drains to direct offsite water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction;</li> <li>Diversion of natural stormwater should be avoided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimise polluted runoff. Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m<sup>3</sup> capacities are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped;</li> <li>The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a site/sediment trap. The sediment/silt traps should be incorporated in the permanent drainage channels to enhance deposition rates;</li> <li>The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94. The detailed design of the sand/silt traps shall be undertaken by the contractor prior to the commencement of construction;</li> <li>Construction works should be programmed to minimise surface excavation works during the rainy seasons (April to September). All exposed earth areas should be</li> </ul>					Implemented	



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
	<ul style="list-style-type: none"> <li>Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts;</li> <li>All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby;</li> <li>Regular environmental audit on the construction site should be carried out in order to prevent any malpractices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the water bodies, marsh and ponds;</li> <li>Adopt best management practices.</li> </ul>						<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p>
S6.4.4.4 – S6.4.4.5	<p><u>Sewage from workforce</u></p> <ul style="list-style-type: none"> <li>Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance;</li> <li>Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project;</li> <li>Regular environmental audit on the construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site.</li> </ul>	To minimise water quality from sewage effluent	Contractor	All construction sites where practicable	Construction phase	<ul style="list-style-type: none"> <li>Water Pollution Control Ordinance</li> <li>TM-DSS</li> </ul>	<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p>
S6.4.4.6	<p><u>Operation of Barging Point at Siu Lam</u></p> <ul style="list-style-type: none"> <li>All barges should be fitted with tight bottom seals to prevent leakage of materials during transport;</li> <li>Barges or hoppers should not be filled to a level that will cause overflow of materials or polluted water during loading or transportation;</li> <li>All vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; and</li> <li>Loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water.</li> <li>Mitigation measures for land-based activities as outlined in Section 6.4.4 should be applied to minimise water quality impacts from site runoff and open stockpile spoils at the proposed barging facilities where appropriate.</li> </ul>	To minimise water quality from operation of barging point at Siu Lam	Contractor	All construction sites where practicable	Construction phase	<ul style="list-style-type: none"> <li>Water Pollution Control Ordinance</li> <li>TM-DSS</li> </ul>	<p>No Applicable.</p> <p>* Barging point at Siu Lam is not in used.</p>
<b>Water Quality (Operational Phase)</b>							



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S7.3.4.3	<p><u>Waste Reduction Measures</u></p> <p>Waste reduction is best achieved at the planning and design phase, as well as by ensuring the implementation of good site practices. The following recommendations are proposed to achieve reduction:</p> <ul style="list-style-type: none"> <li>segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>proper storage and site practices to minimise the potential for damage and contamination of construction materials;</li> <li>plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste;</li> <li>sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete metal etc.);</li> <li>provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling.</li> </ul>	Reduce waste generation	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>	Implemented Implemented Implemented Implemented Implemented
S7.3.4.5	<p><u>Storage of Waste</u></p> <p>The following recommendation should be implemented to minimise the impacts:</p> <ul style="list-style-type: none"> <li>non-inert C&amp;D materials such as soil should be handled and stored well to ensure secure containment;</li> <li>stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away;</li> <li>different locations should be designated to stockpile each material to enhance reuse;</li> </ul>	Good site practice to minimise the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Land (Miscellaneous Provisions) Ordinance</li> <li>Waste Disposal Ordinance</li> <li>ETWB TCW No. 19/2005</li> </ul>	Implemented Implemented Implemented
S7.3.4.6	<p><u>Collection and Transportation of Waste</u></p> <p>The following recommendation should be implemented to minimise the impacts:</p> <ul style="list-style-type: none"> <li>remove waste in timely manner;</li> <li>employ the trucks with cover or enclosed containers for waste transportation;</li> <li>obtain relevant waste disposal permits from the appropriate authorities; and</li> <li>disposal of waste should be done at licensed waste disposal facilities.</li> </ul>	Minimise waste impacts from storage	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>	Implemented Implemented Implemented Implemented
S7.3.4.8 – S7.3.4.15	<p><u>Excavated and C&amp;D Materials</u></p> <p>Wherever practicable, C&amp;D materials should be segregated from other wastes to avoid contamination and ensure acceptability at public filling areas or reclamation sites. The following mitigation measures should be implemented in handling the excavated and C&amp;D materials:</p> <ul style="list-style-type: none"> <li>maintain temporary stockpiles and reuse excavated fill material for backfilling;</li> <li>carry out on-site sorting;</li> <li>make provisions in the Contract documents to allow and promote the</li> </ul>	Minimise waste impacts from excavated and C&D materials	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Land (Miscellaneous Provisions) Ordinance</li> <li>Waste Disposal Ordinance</li> </ul>	Implemented Implemented Implemented Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
	<ul style="list-style-type: none"> <li>use of recycled aggregates where appropriate; and</li> <li>implement a recording system for the amount of waste generated, recycled and disposed of for checking.</li> <li>The recommended C&amp;D materials handling should include: <ul style="list-style-type: none"> <li>On-site sorting of C&amp;D materials;</li> <li>Reuse of C&amp;D materials; and</li> <li>Use of Standard Formwork and Planning of Construction Material purchasing.</li> </ul> </li> </ul>						<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p>
S7.3.4.17 – S7.3.4.18	<p><u>Chemical Waste</u></p> <p>If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producer. Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste Contractor. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.</p>	Control the chemical waste and ensure proper storage, handling and disposal.	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal (Chemical Waste)</li> <li>Code of Practice on the Packaging, Labelling and Storage of Chemical Waste</li> </ul>	Implemented
S7.3.4.19	<p><u>General Refuse</u></p> <ul style="list-style-type: none"> <li>General refuse should be stored in enclosed bins separately from construction and chemical wastes. Recycling bins should also be placed to encourage recycling.</li> <li>Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean.</li> <li>A reputable waste collector should be employed to remove general refuse on a daily basis.</li> </ul>	Minimise production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>	<p>Implemented</p> <p>Implemented</p> <p>Implemented</p>
S7.3.4.20	<p><u>Sewage</u></p> <ul style="list-style-type: none"> <li>The WMP should document the locations and number of portable chemical toilets depending on the number of workers, land availability, site condition and activities.</li> <li>Regularly collection by licensed collectors should be arranged to minimise potential environmental impacts.</li> </ul>	Minimise production of sewage impacts	Contractor	All construction sites	Construction phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>	<p>Implemented</p> <p>Implemented</p>
<b>Waste Management (Operational Waste)</b>							
S7.4.4.1	<p><u>General Refuse</u></p> <p>A reputable waste collector should be employed to remove general refuse on a daily basis.</p>	Remove general refuse during routine road cleaning activities on the roads network and avoid odour, pest and litter impacts	Highways Department /Contractor	Roads network for the C&C facilities and Lin Ma Hang Road	Operational phase	<ul style="list-style-type: none"> <li>Waste Disposal Ordinance</li> </ul>	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
<b>Land Contamination</b>							
S8.9.1.1	Re-appraisal of the potentially contaminated site (SRC-1)	Identify any hot spots for SI within the southeast and western portions of SRC-1	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	Once the works area for the Project is confirmed and site access is available (e.g. after land resumption)	<ul style="list-style-type: none"> <li>Annex 19 of the TM-EIAO, Guidelines for Assessment of Impact On Sites of Cultural Heritage and Other Impacts (Section 3 :Potential Contaminated Land Issues);</li> <li>Guidance Manual for Use of Risk-Based Remediation Goals (RBRGs) for Contaminated Land Management;</li> <li>Guidance Notes for Contaminated Land Assessment and Remediation; and</li> <li>Practice Guide for Investigation and Remediation of Contaminated Land</li> <li>Recommendations in Health Risk Assessment</li> </ul>	Implemented
S8.11.1.1	Preparation and submission of Contamination Assessment Plan (CAP) to EPD for review and approval, if required	Present the findings of the reappraisal and strategy of the recommended SI, if required	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	After land resumption and prior to the construction phase	Ditto	Implemented
S8.11.1.2	Preparation and submission of Contamination Assessment Report (CAR) to EPD for review and approval, if required	Present the findings of SI, if any, and evaluate the level and extent of potential contamination	Project Proponent / Detailed Design Consultant	Potentially contaminated site (SRC-1)	Prior to the construction phase	Ditto	Implemented
S8.11.1.2	Preparation and submission of Remediation Action Plan (RAP) to EPD for review and approval if contamination is identified	Recommend appropriate mitigation	Project Proponent /	Potentially contaminated	Prior to the construction	Ditto	Not required as no contamination is

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S8.11.1.2	Preparation and submission of Remediation Report (RR) to EPD for review and approval following the completion of any necessary remediation works	measures for the contaminated soil and groundwater identified in the assessment if remediation is required Demonstrate that the decontamination work is adequate and is carried out in accordance with the endorsed CAR and RAP	Detailed Design Consultant Project Proponent / Detailed Design Consultant	site (SRC-1) Potentially contaminated site (SRC-1)	phase Prior to the construction phase	Ditto	identified. Not required as no contamination is identified.
<b>Ecology ( Construction Phase)</b>							
S9.7.2.3	Preparation and submission of Upland Grassland Reinstatement Plan to EPD for agreement.	An Upland Grassland Reinstatement Plan will be prepared by a qualified ecologist/botanist with full details of the findings of a baseline grassland survey, the practical details and methodology of the physical excavation, transport and storage or turves/topsoil and their subsequent reinstatement once the receptor sites have been established, along with an implementation programme of reinstatement, post-reinstatement monitoring and maintenance programme. A contingency plan	Project Proponent/ Detailed Design Consultant (qualified ecologist/botanist) for Upland Grassland Reinstatement Plan	Engineered slopes Of Crematorium Indicative locations for Grassland Reinstatement should be referred to <b>Figure 9.11</b> of the EIA Report	Prior to construction phase	<ul style="list-style-type: none"> <li>Reinstatement and establishment requirements to be detailed in Upland Grassland Reinstatement Plan</li> <li>TM-EIAO</li> </ul>	Implemented *Upland Grassland Reinstatement Plan was submitted to EPD.

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
		<p>should be proposed in the Grassland Reinstatement Plan so as to describe the action and limit levels and the action plan if certain performance criteria (such as area of preferred habitat) are not met during the monitoring and maintenance period.</p>					
<p>S9.7.2.5 – S9.7.2.6</p>	<p>Preparation and submission of a Vegetation Survey Report and Transplantation Proposal (if needed as concluded in the Vegetation Survey Report) to EPD for agreement.</p>	<p>The Vegetation Survey will report the presence, as well as update the conditions, number, locations and habitat types of any identified floral species of conservation importance to be impacted by the development, and evaluate suitability and/or practicality of transplantation.</p> <p>The Transplantation Proposal will recommend locations of the receptor site(s), transplantation methodology, implementation programme of transplantation and post-transplantation monitoring</p>	<p>Project Proponent/ Detailed Design Consultant (qualified ecologist/botanist) for Vegetation Survey Report and Transplantation Proposal.</p>	<p>Within the Project Area where applicable</p>	<p>Prior to construction phase</p>	<ul style="list-style-type: none"> <li>Survey findings and transplantation methodology to be detailed in Vegetation Survey Report and Transplantation Plan respectively.</li> <li>TM-EIAO.</li> </ul>	<p>Implemented * Vegetation Survey Report and Transplantation Proposals for Contract 1 and Contract 2 were submitted to EPD.</p>

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S9.7.5.3 – S9.7.5.5, S9.8.1.6	Preparation and submission of Enhancement Woodland Proposal to EPD for agreement.	and maintenance programme.  Recommend appropriate enhancement planting programme, planting and post-transplantation monitoring methodology, action plan for monitoring the enhancement planting and maintenance programme.	Project Proponent/ Detailed Design Consultant (qualified ecologist/botanist) for Wooded Area Proposal.	Filled slope west of the platform, and north west of the platform in the valley below MacIntosh Fort Indicative locations for Enhancement Woodland should be referred to <b>Figure 9.11</b> of the EIA Report	Prior to construction phase	<ul style="list-style-type: none"> <li>Enhancement planting and establishment requirements to be detailed in Wooded Enhancement Proposal.</li> <li>TM-EIAO</li> </ul>	Implemented *Woodland compensation plan was submitted to EPD.
S9.7.3.1 – S9.7.3.3	Indirect impacts due to potential changes in water quality, hydrology and sedimentation could occur to a series of downstream watercourses and wetland systems (including the wet woodland, marsh and mitigation ponds) during both the construction (for the Platform and LMHR widening works) and operational stages.  Generally, indirect water impact to any aquatic fauna during the construction phase should easily be avoided by implementing water control measures (ETWB TCW No. 5/2005) to avoid direct or indirect impacts any watercourses and good site practices (further details are discussed in Section 6 of the EIA Report).  In addition, construction phase impacts on the watercourses, riparian corridor and fauna using these areas will be minimised by erection of a 2m high, solid, dull green site boundary fence on the edge of any active works area, 30m from the watercourse. Where this is not practicable due to site constraints, demarcation fencing will need to be erected to prevent unauthorised encroachment into the riparian corridor by constructions works and traffic. Detailed mitigation measures will be designed at the detailed design stage.	Minimise the indirect impacts to Water Quality and Hydrology	Contractor /detailed design consultant.	On the edge of any active works area, 30m from The watercourse	Prior to commencement and during construction phase	<ul style="list-style-type: none"> <li>ETWB TCW No. 5/2005</li> <li>TM-EIAO</li> </ul>	Implemented.

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S9.7.3.4 – S9.7.3.6	<p>Mitigation for noise disturbance (details refer to S5.5.5 to S5.6.6 of this table). Site formation and construction are tentatively proposed to cover a 65-month period from mid 2017 to late 2022.</p> <p>As a precautionary approach, consideration should be given at the detailed design stage to avoid the use of highly reflective materials in the design and implementing the use of opaque materials, fritting, breaking up external reflections with stickers or plastic wrap and/or any other birdfriendly design for noise barriers.</p> <p>Works will be restricted to daytime and any construction lighting should be designed and positioned as to not impact on adjacent ecologically sensitive areas.</p>	<p>The construction work and site formation will be phased in order to reduce overall noise disturbance impacts in particular areas. Collisions usually occurs as a result of birds perceiving a clear path through an object that is transparent or appears to be transparent at some distance, or if the noise barrier is highly reflective which would appear to be composed of the adjacent natural vegetation. Furthermore, mitigation measures to control noise disturbance during this phase will involve the selection of quieter plant, use of movable noise barriers and erection of hoarding and fencing to demarcate the site boundary</p>	Contractor Project Proponent	All construction sites	Prior to commencement and during construction phase	<ul style="list-style-type: none"> <li>• TM-EIAO.</li> </ul>	
.9.7.3.7	<p>In order to demonstrate ecological awareness and to minimise the risk of indirect impacts from water pollution and hill fires, a series of good site practices should be adopted by site staff throughout the construction phase at each works site. These are as follows:</p> <ul style="list-style-type: none"> <li>• Put up signs to alert site staff about any locations which are ecologically sensitive and measures to prevent accidental impacts;</li> <li>• Erection of temporary geotextile silt or sediment fences/oil traps around any earth-moving works to trap any sediments and prevent them from entering</li> </ul>	<p>Minimise impacts on hydrological condition and water quality of hillside watercourses and reduce chances of hillfires.</p>	Contractor	All construction sites	Prior to commencement and during construction phase	<ul style="list-style-type: none"> <li>• TM-EIAO.</li> </ul>	<p>Implemented</p> <p>Implemented</p>

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
	<p>watercourses;</p> <ul style="list-style-type: none"> <li>Prohibition of soil storage against trees or close to waterbodies;</li> <li>Delineation of works site to prevent encroachment onto adjacent habitats and fence off areas which have some ecological value;</li> <li>No smoking, hot works or sources of fire close to upland grassland;</li> <li>No on-site burning of waste; and</li> <li>Waste and refuse in appropriate receptacles.</li> </ul>						<p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p> <p>Implemented</p>
S.9.7.3.9	<p>Precautionary checks by a suitably experienced ecologist of the vegetation for the presence of nesting birds should be carried out in the breeding season (February to July) before vegetation clearance. These impacts can be avoided by conducting vegetation clearance during the non-breeding season (tentatively August-January) and phased through the project period to minimise impacts.</p>	<p>Minimise the impacts to breeding birds within the works areas.</p>	Contractor	All construction sites	Prior to site clearance	<ul style="list-style-type: none"> <li>TM-EIAO</li> <li>WAPO</li> </ul>	<p>Implemented during breeding season.</p>
<b>Ecology (Operational Phase)</b>							
S9.7.2	<p>Establishment, maintenance and monitoring of a Upland Grassland Reinstatement Area</p>	<p>Reinstatement of upland grassland and to maintain connectivity in Sandy Ridge.</p>	Project Proponent/ Contractor / Maintenance Authority	<p>Engineered slopes of Crematorium</p> <p>Indicative locations for Grassland Reinstatement should be referred to <b>Figure 9.11</b> of the EIA Report</p>	Operational phase	<ul style="list-style-type: none"> <li>Monitoring methodology and successfulness of survival of upland grassland should follow Upland Grassland Reinstatement Plan.</li> <li>TM-EIAO.</li> </ul>	<p>Upland Grassland Reinstatement Area will be implemented by other contract.</p>
S9.7.5.3 – S9.7.5.6	<p>Establishment, maintenance and monitoring of an enhancement woodland</p>	<p>Recommend appropriate enhancement planting programme, planting and post-transplantation monitoring methodology, action plan for monitoring the enhancement planting and</p>	Project Proponent/ Detailed Design Consultant (qualified ecologist/ botanist) for Wooded Area Proposal.	<p>Filled slope west of the platform, and north west of the platform in the valley below MacIntosh Fort</p>	Operational phase	<ul style="list-style-type: none"> <li>Enhancement planting and establishment requirements to be detailed in Wooded Area Proposal.</li> <li>TM-EIAO.</li> </ul>	

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
		maintenance programme.		Indicative locations for Enhancement Woodland should be referred to <b>Figure 9.11</b> of the EIA Report			
S9.7.4.1 – S9.7.4.5	<p><u>Mitigation for Impacts to Water Quality and Hydrology (Operational Phase)</u></p> <ul style="list-style-type: none"> <li>Stormwater drainage system will be further developed in detailed design stage to collect dusty materials from water collected from the platform and associated road system. Silt traps will be installed to ensure removal of dusty materials. Regular cleaning will be conducted to avoid debris entering downstream rivers during first flush; and</li> <li>The proposed small diameter bore pile system at the foundation of the proposed platform structure.</li> </ul>	<p>Specific mitigation measures will be implemented to prevent indirect impacts wetland habitats and fauna. Mitigation measures are to be further developed in the detailed design stage to address any water quality impacts due to the drainage from the proposed platform, and any erosion issues due to the drainage from the proposed platform. The surface runoff collected on the platform will be captured by a stormwater drainage system, which will be further developed at the detailed design stage. The proposed small diameter bore pile system at the foundation of the</p>	Detailed Design Consultant	Wet woodland (and further down the marsh and mitigation ponds) and the seasonal watercourse to the east of the Project boundary	Detailed Design phase/Operational phase	<ul style="list-style-type: none"> <li>TM-EIAO</li> </ul>	Implemented before Operational phase

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
		proposed platform structure would allow a notional free area of about 87 – 91% for groundwater to pass through.					
S9.7.4.6	Minimise the potential indirect light disturbance on the Street Lighting on fireflies surrounding the Project Site during operational phase	Reduce light pollution and impact on the nearby habitats and their associated wildlife groups, particularly nocturnal fireflies.	Detailed Design/ Consultant/ Operator	The whole Project area	Detailed Design phase/Operational phase	• TM-E/IAO	Implemented before Operational phase
S9.7.4.7	<ul style="list-style-type: none"> <li>It is considered that at the detailed design stage, street lighting of similar lux/light intensity as to what is currently present is utilised.</li> </ul> Furthermore, as a precautionary measure, it is suggested that deflectors are fixed to the back of the street lights to prevent additional light reaching the marsh and causing adverse impacts to fireflies.						
S9.7.4.9	The increase in visitors to the columbarium allows greater public access to the upland grassland of Sandy Ridge and in turn, the potential for hill fires is also increased. Fires may emanate from discarded cigarettes and from specific practices during festivals or grave-sweeping.	Minimise the risk of hill fires.	Detailed Design/ Consultant/ Operator	The whole Project area	Detailed Design phase/Operational phase	• TM-E/IAO	Implemented before Operational phase
S9.7.4.9	In order to reduce the risk of hill fires, sufficient educational signage should be displayed throughout the columbarium warning people of the risks of fire and strictly prohibits practices that could cause hill fires. This will require input in the detailed design phase.						
<b>Fisheries</b>							
S10.5.1.1	No loss of fish ponds is anticipated and no <i>in situ</i> mitigation is required. However, mitigation measures for water quality (S6.4.4 – S6.5.4 in this table) proposed are also pertinent in ensuring that fisheries impacts of the Project do not occur downstream of the Project area either locally or in Inner Deep Bay.	-	-	-	-	-	Not applicable
<b>Landscape &amp; Visual</b>							
S11.8.1.3, Table 11.9	CM1 – The construction area and contractor's temporary works areas should be minimised to avoid impacts on adjacent landscape, and the reliance on off-site construction.	Minimise landscape impact and visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-	Implemented.



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S11.8.1.3, Table 11.9	CM3 – Screening of construction works by hoardings/noise barriers around works area in visually unobtrusive colours and to screen construction works. It is proposed that screening be compatible with the surrounding environment and non-reflective, recessive colours be used. Hoarding should be taken down at the end of the construction period.	Minimise visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-	Implemented.
S11.8.1.3, Table 11.9	CM4 – Dust and Erosion Control for Exposed Soil - Excavation works and demolition of existing building blocks shall be well planned with precautions to suppress dust. Exposed soil shall be covered or watered often. Areas that are expected to be left with bare soil for a long period of time after excavation shall be properly covered with suitable protective fabric. Suitable drainage shall be provided around construction sites to avoid discharge of contaminants and sediments into sensitive water-based habitat.	Minimise indirect landscape impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-	Implemented.
S11.8.1.3, Table 11.9	CM5 – Control night-time lighting and glare by hooding all lights.	Minimise visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	-	Implemented.
11.8.1.3, Table 11.9	CM6 – Tree Protection and Preservation – Woodland, plantation and other vegetation within the Study Area will be protected and preserved as far as possible in accordance with ETWB TCW No. 29/2004 - Registration of Old and Valuable Trees, and Guidelines for their Preservation and DEVB TCW No.07/2015 – Tree Preservation. Detailed Design Considerations are made to avoid impacts to trees, e.g. proper viaduct/ bridge design routing to avoid majority of the woodland, locating the columbarium buildings in areas with less trees and ensuring design of the buildings has as small a footprint as practical.	Minimise landscape impact and visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Construction phase	<ul style="list-style-type: none"> <li>• DEVB TC(W) 07/2015</li> <li>• Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DevB</li> </ul>	Implemented.
S11.8.1.3, Table 11.9	CM7 – Tree Transplantation – Tree(s) will be affected according to the Tree Preservation and Removal Proposal to be carried out in a later stage. Established trees of value are to be re-located where practically feasible.	Minimise landscape and visual impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Design and Construction phase	<ul style="list-style-type: none"> <li>• ‘Guidelines for Tree Risk Management And Assessment Arrangement on an Area Basis and on a Tree Basis’, issued January 2011, Greening, Landscape and Tree Management</li> </ul>	Implemented.

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S11.8.1.3, Table 11.9	CM8 - Implementing precautionary control measures during construction stage accordingly to ETWB TCW No. 5/2005 – Protection of natural streams/rivers from adverse impacts arising from construction works to avoid direct or indirect impacts any watercourses and good site practices.	Minimize landscape impact	Funded by CEDD and implemented by Contractor	Work site/ during construction	Design and Construction phase	(GLTM) Section, DevB <ul style="list-style-type: none"> <li>• Latest recommended horticultural practices from GLTM Section, DevB</li> <li>• ETWB TCW No. 5/2005 – Protection of natural streams/rivers from adverse impacts arising from construction works</li> </ul>	Implemented.
S11.8.1.3, Table 11.9	OM1 – Compensatory Woodland Planting - The arrangement of compensatory planting (e.g. areas of woodland to be compensated and space to be allowed within the Project Site) will be subject to detailed engineering design, landscape design and planting plan, and is recommended to be implemented prior to the construction activities as far as practical.	Compensate the loss of landscape greenery and enhance the overall visual value of the site.	Funded by CEDD and implemented by Contractor	Within Project Site	Prior to Construction phase	<ul style="list-style-type: none"> <li>• DEVB TC(W) 07/2015 – Tree Preservation</li> <li>• Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DevB</li> <li>• DEVB TCW No. 06/2015 – Maintenance of Vegetation and Hard Landscape Features</li> </ul>	Implemented
S11.8.1.3, Table 11.9	OM2 – Compensatory Tree Planting for Plantation and Other Vegetated Areas - Compensatory planting should be provided in accordance with DEVB TCW No. 07/2015 to compensate for those trees felled. According to the preliminary design, compensatory trees will be planted on the cut/fill slopes, along new roads and in car parks. The selection of planting species shall be made with reference to the species identified in the future Detailed Tree Survey and be native to Hong Kong or the South China region.	Compensate the loss of landscape greenery and enhance the overall visual value of the site.	Funded by CEDD and implemented by Contractor	Within Project Site	Construction phase	<ul style="list-style-type: none"> <li>• DEVB TC(W) 07/2015 – Tree Preservation</li> <li>• Latest recommended horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DevB</li> <li>• DEVB TCW No. 06/2015 –</li> </ul>	Implemented



EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S11.8.1.3, Table 11.9	OM3 – Amenity Planting and aesthetic streetscape design of hard landscaping for Pedestrian Walkway, Roadside - Roadside amenity planting should be provided along Sha Ling Road, Lin Ma Hang Road, as well as the internal road within Sandy Ridge columbarium and crematorium site; to enhance the landscape quality of the existing and proposed transport routes. Climbers are proposed to cover vertical, hard surfaces of the piers of the proposed viaducts, and also the newly formed retaining wall within the site. Shade tolerant plants will be planted, where light is sufficient, to improve aesthetic value of areas under viaducts.	Minimise visual impact and also enhance landscape.	Funded by CEDD and implemented by Contractor	Within Project Site	Construction phase	Maintenance of Vegetation and Hard Landscape Features  • Guidelines on Greening of Noise Barriers, issued April 2012, GLTMS, DevB • DEVB TCW No. 06/2015 – Maintenance of Vegetation and Hard Landscape Features	Implemented
S11.8.1.3, Table 11.9	OM4 – Greening Works and Contour Grading Works on Cut/Fill Slopes - Greening works such as hydroseeding/ terraces of shrub or tree planting will be provided where slope gradient allows, according to Geotechnical Engineering Office (GEO) Publication No.1/2011 Technical Guidelines on Landscape Treatment for Slopes.	Minimise landscape and visual impact	Funded by CEDD and implemented by Contractor	Within Project Site	Construction phase	Geotechnical Engineering Office (GEO) Publication No.1/2011 Technical Guidelines on Landscape Treatment for Slopes.	Implemented
S11.8.1.3, Table 11.9	OM5 – Landscape design treatment to be provided by relevant government department.	Mitigate the loss of greenery and enhance the overall landscape and visual value	Funded by FEHD and implemented by Contractor	Within Project Site	After handover to the relevant department	-	Implemented after handover to the relevant department
S11.8.1.3, Table 11.9	OM6 – Architectural and chromatic treatment of the hard architectural and engineering structures and facilities.	Mitigate the loss of greenery and enhance the overall landscape and visual value	Funded by FEHD and implemented by Contractor	Within Project Site	After handover to the relevant department	-	Implemented after handover to the relevant department
S11.8.1.3, Table 11.9	OM7 – Aesthetic design of the proposed noise barriers.	Mitigate the visual impact	Funded by CEDD and implemented by Contractor	Along Sha Ling Road and Lin Ma Hang Road	Construction phase	• WBTC No. 36/2004 - ACABAS - submission is required to ACABAS for approval of any bridges and associated structures within the public highway	Implemented

EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
S11.8.1.3 , Table 11.9	OM8 - Silt traps should also be incorporated into design of road gullies for the natural water stream(s).	Minimise the landscape impact on natural stream	Funded by CEDD and implemented by Contractor	Within Project Site	Construction Phase	system.	Implemented
<p>Notes:</p> <p>(a) A detailed Tree Survey Report showing all identified valuable trees and OVT will be undertaken in a separate Tree Preservation and Removal Proposal.</p> <p>(b) Wood resulting from tree removal should be recycled as mulch or soil conditioner for re-use within the Project or in other projects as far as possible e.g. for the construction of soft landscape work, were practical.</p> <p>(c) Contractor is responsible for landscaping during the agreed establishment and maintenance period. Other designated management and maintenance agents to take up maintenance and management of landscaping after end of agreed period</p> <p>(d) Highways Department (HyD) is responsible for maintenance and management of landscaping of public road side slope, Leisure and Cultural Services Department (LCS D) is responsible for the management and maintenance of soft landscapes along non-expressway public roads outside Country Park and Food and Environmental Hygiene Department (FEHD) is responsible for landscaping of other areas allocated to FEHD..</p> <p>(e) The landscape mitigation treatment of the future development site shall follow the below frameworks:</p> <ul style="list-style-type: none"> <li>- Buffer planting shall be provided to soften the edge of the site.</li> <li>- Aesthetic landscape treatment including both soft and hard landscape features shall be provided.</li> <li>- Vertical greening shall be provided as far as practicable.</li> <li>- At-grade tree planting shall be provided as far as possible while planting space is allowed, to enhance the overall environment.</li> <li>- Architectural design shall blend in with the surrounding environment.</li> <li>- Overall greening ratio shall comply with TC(W) No.3/2012 Site coverage of Greenery for Government Building Projects.</li> </ul>							
EIA Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and / or standards to be achieved	Implementation status and remark*
<p>The compensatory woodland planting shall be included woodland mixed whips, seeding, and shrubs. The principle of the location shall be the extension of the existing woodland, as well as the original lost woodland location. The proposal will be agreed with AFCD, the woodland enhancement planting shall refer to Chapter 9.</p>							
<b>EM&amp;A Project</b>							
S13.1.1.1	An Independent Environmental Checker needs to be employed as per the EM&A Manual.	Control Performance	Highways Department	All construction sites	Construction phase	• EIAO Guidance Note No.4/2010 • TM-EIAO	Implemented
S13.2.1.1	1) An Environmental Team needs to be employed as per the EM&A Manual.	Perform environmental monitoring & auditing	Highways Department / Contractor	All construction sites	Construction phase	• EIAO Guidance Note No.4/2010 • TM-EIAO	Implemented
S13.4.1.2	2) Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures. 3) An environmental impact monitoring needs to be implementing by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with.						

## **Appendix P**

### **Illustrations of Site Activities**

DO NOT SCALE DRAWING - CHECK ALL DIMENSIONS ON SITE.  
 ALL RIGHTS RESERVED.  
 © UVE ARUP & PARTNERS HONG KONG LIMITED.

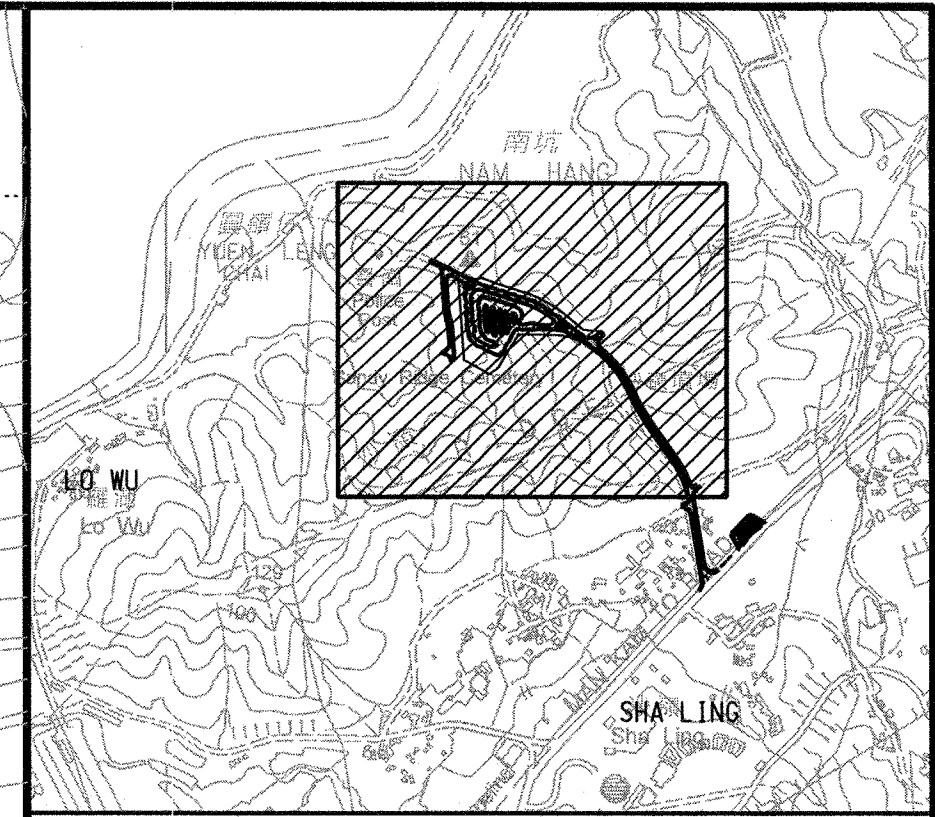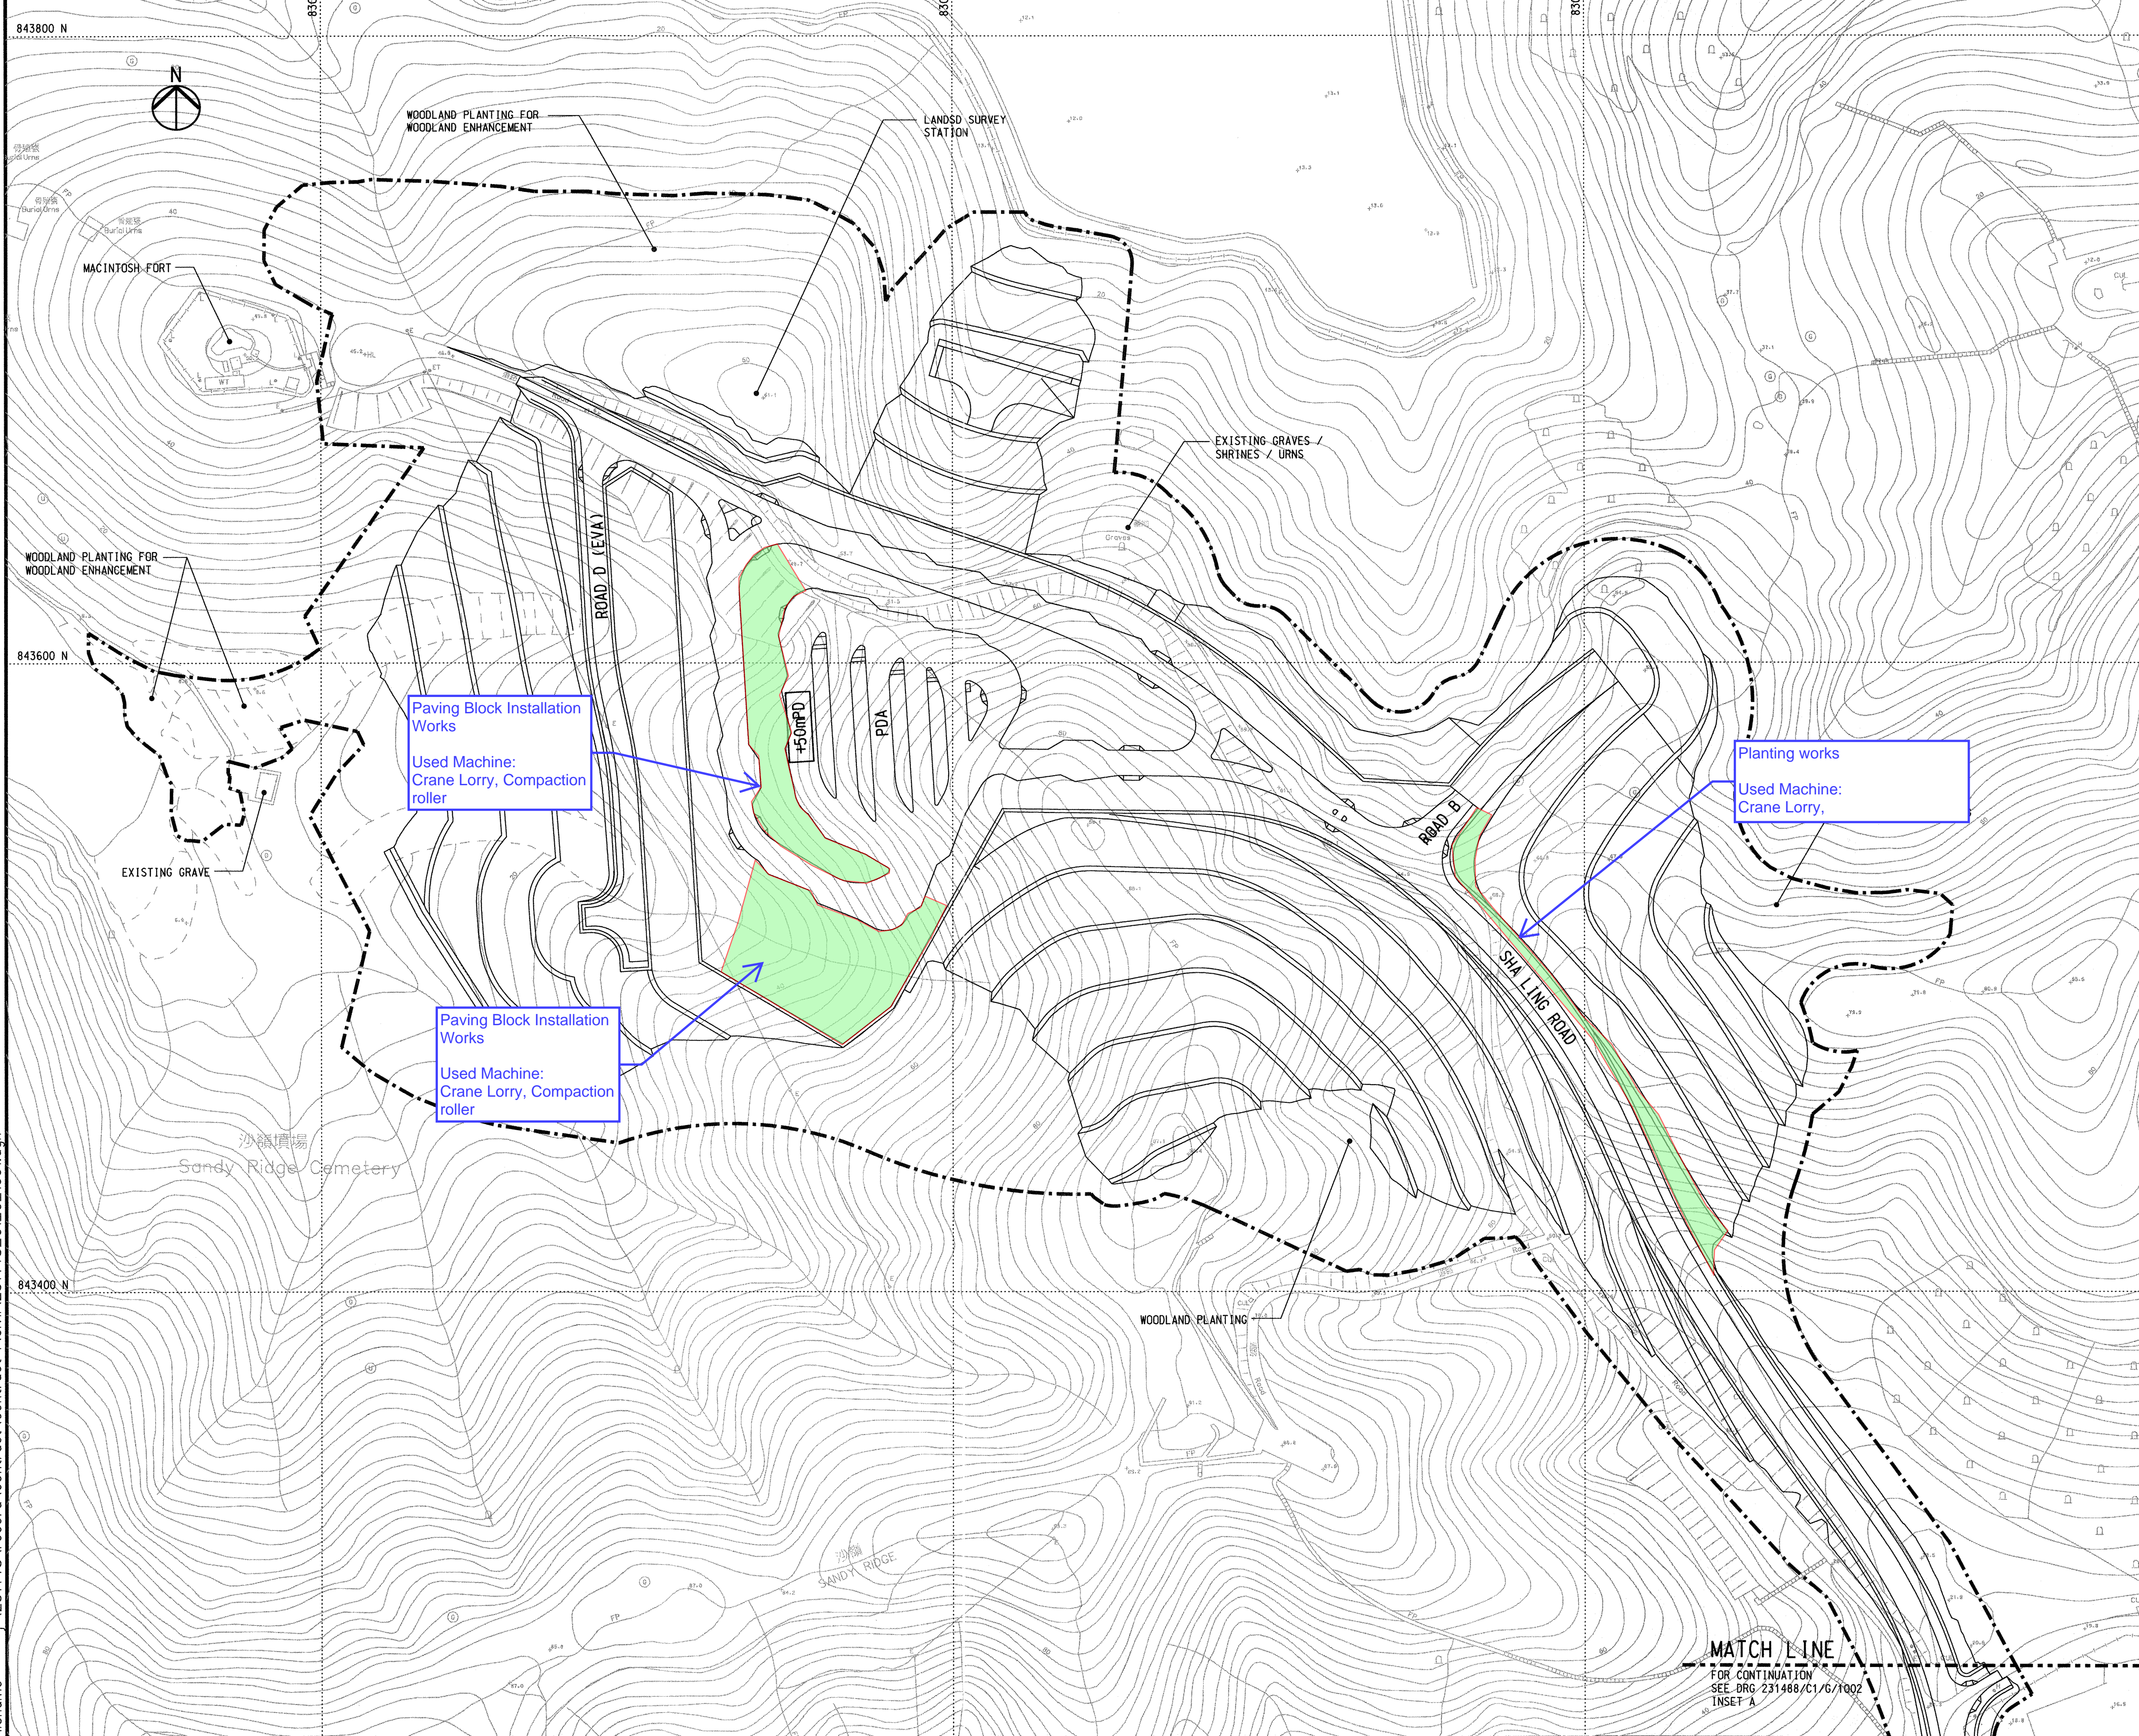

KEY PLAN

**LEGEND:**  
 - - - - - PROPOSED WORKS SITE  
 +50mPD SITE FORMATION LEVEL

Rev	Description	By	Date

Consultant  
**ARUP**

Contract No. and Title:  
 Contract No. CV/2016/10  
 Site Formation and Associated  
 Infrastructural Works for  
 Development of Columbarium at  
 Sandy Ridge Cemetery





Drawing title  
**GENERAL LAYOUT  
 (SHEET 1 OF 3)**

Drawing no. 231448/C1/G/1001		Rev. -	
Drawn WM	Date 12/16	Checked AW	Approved DL
Scale 1:1000 @A1		Status CONTRACT	

COPYRIGHT RESERVED  
 土木工程拓展署  
 Civil Engineering and  
 Development Department

Printed by : 11/27/2017  
 Filename : i:\231448\record\contract\1\civil\231448\_C1\_G\_1001.dgn

MATCH LINE  
 FOR CONTINUATION  
 SEE DRG 231448/C1/G/1002  
 INSET A

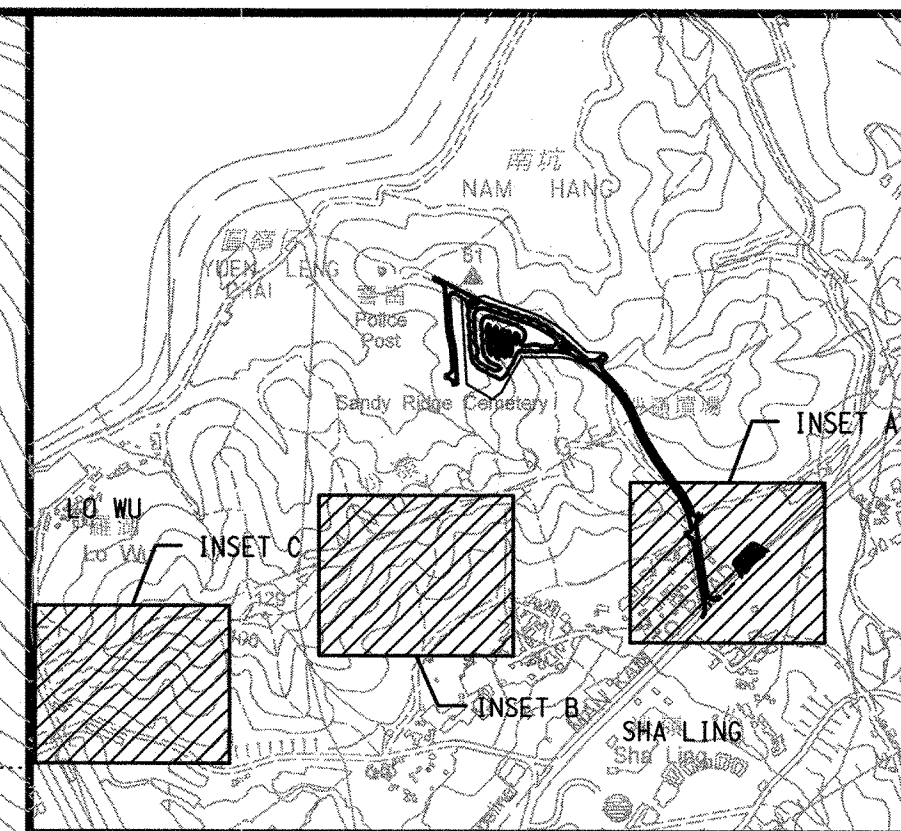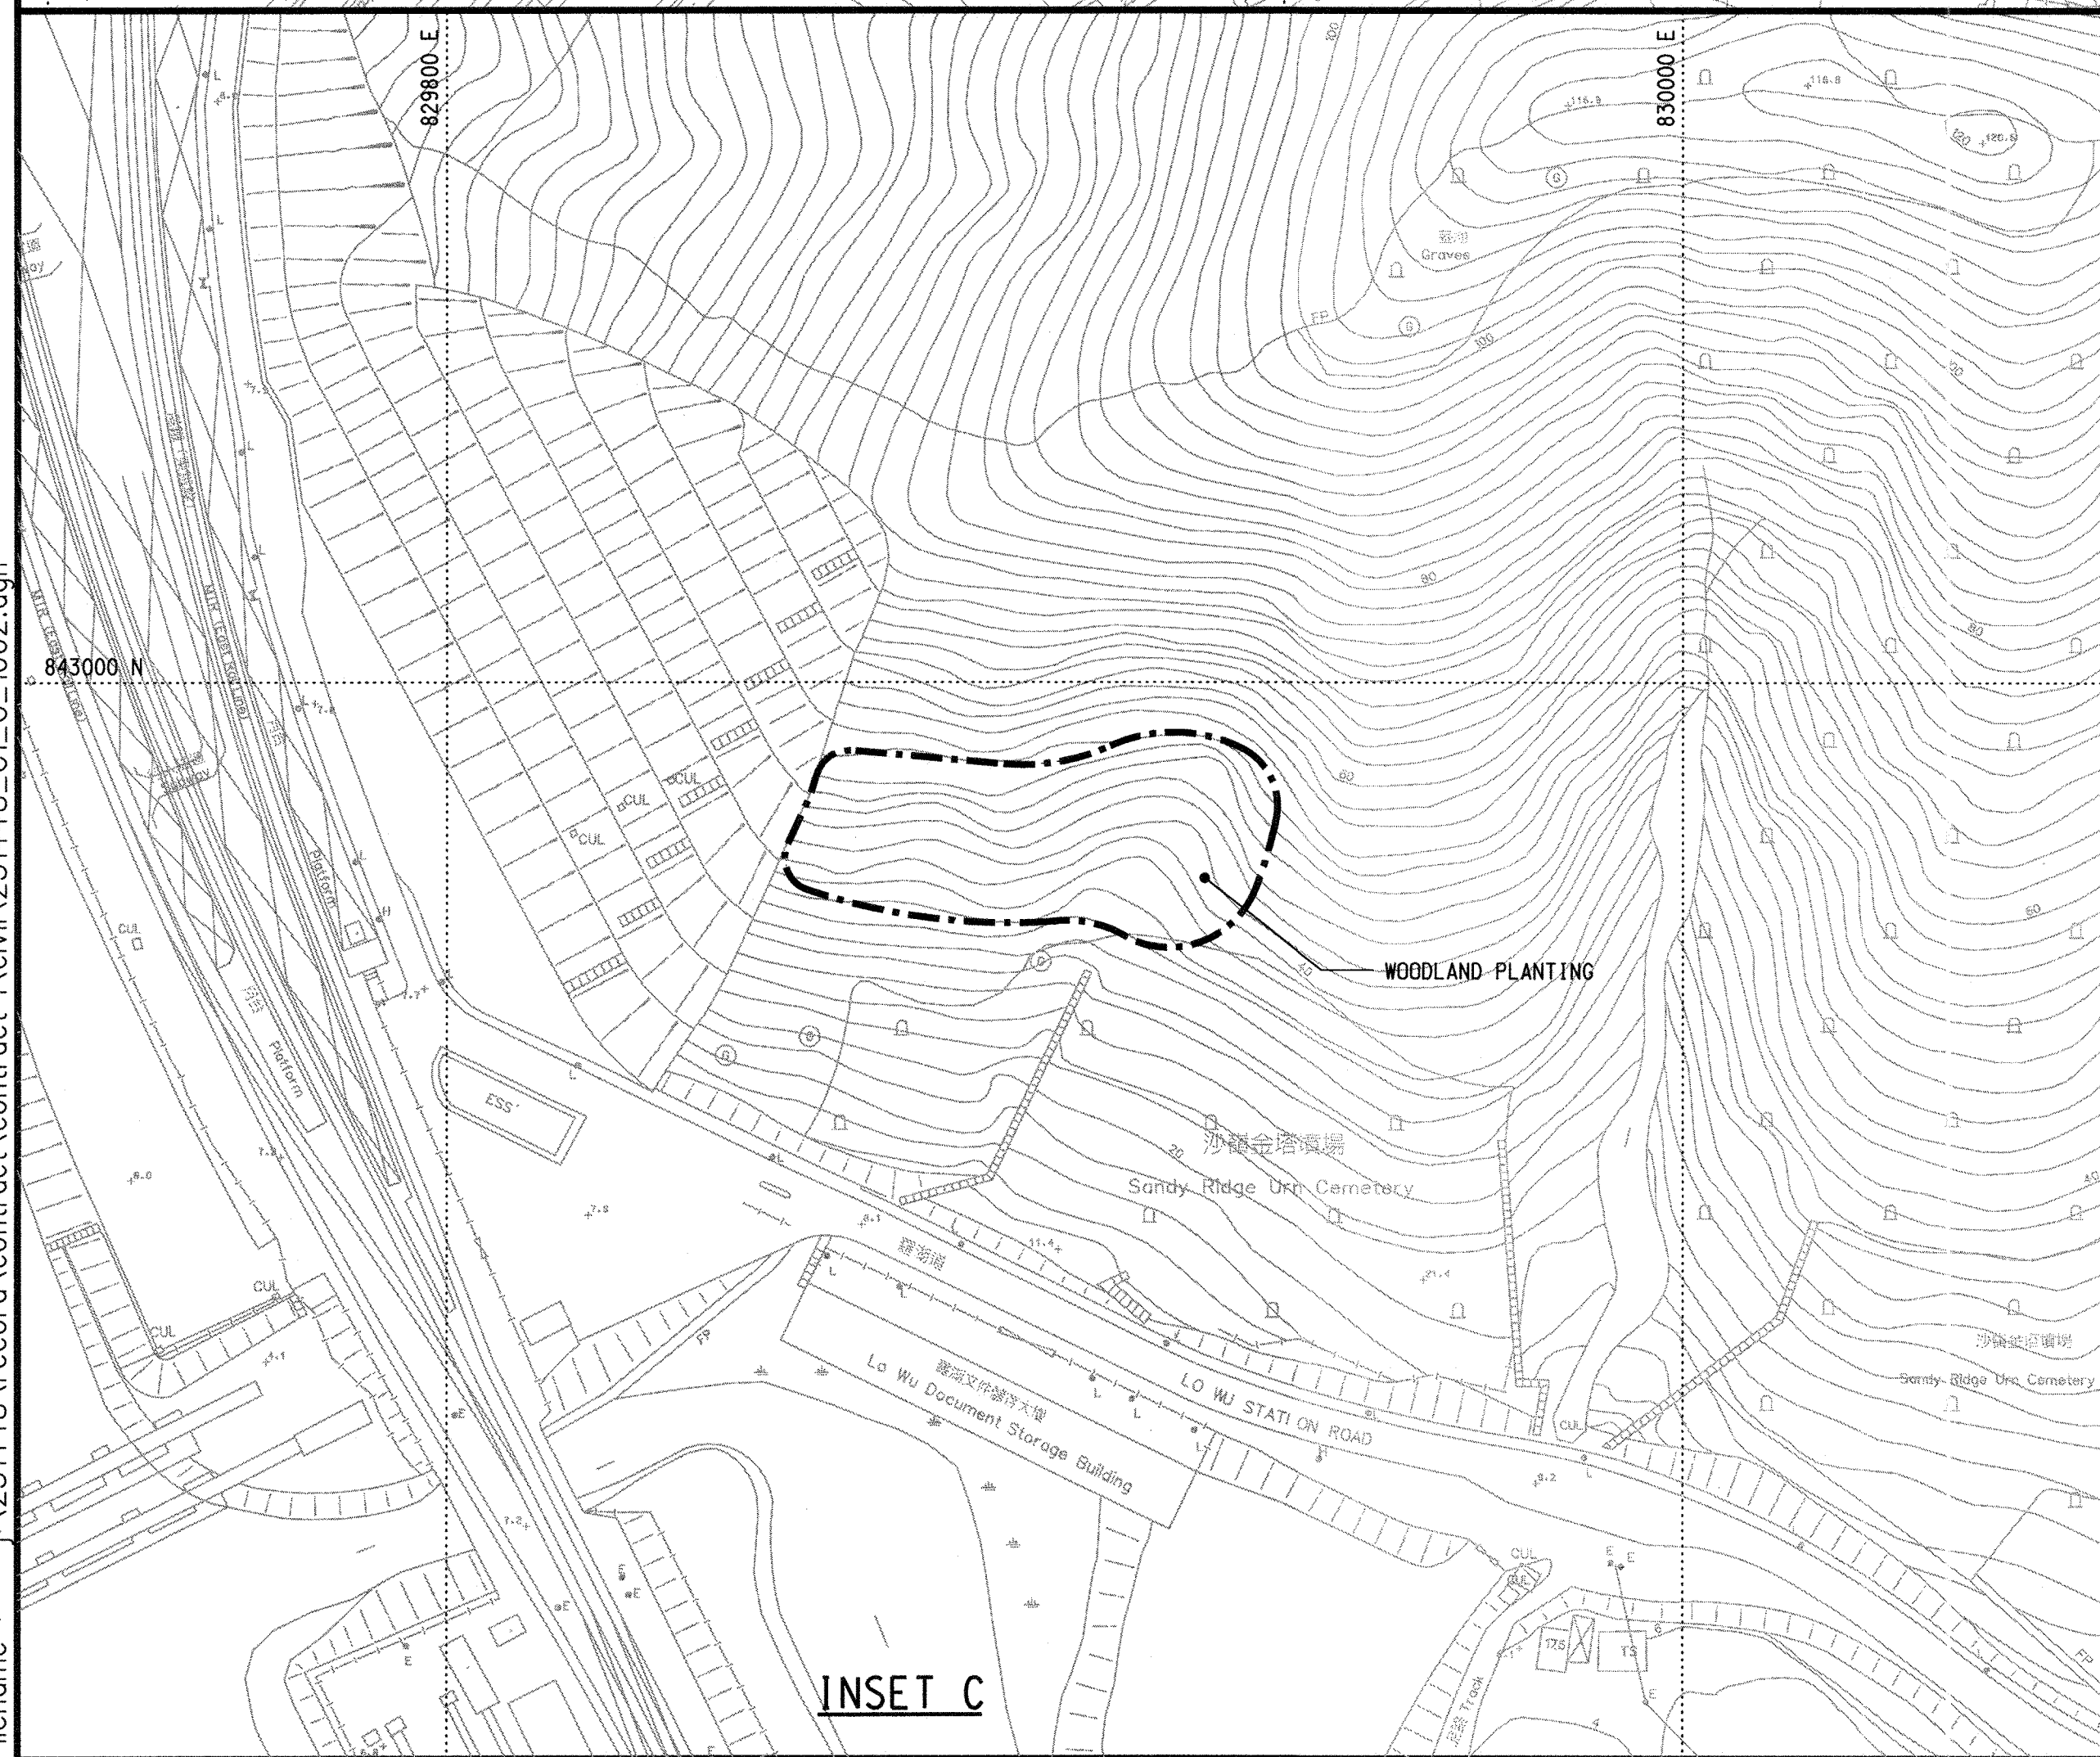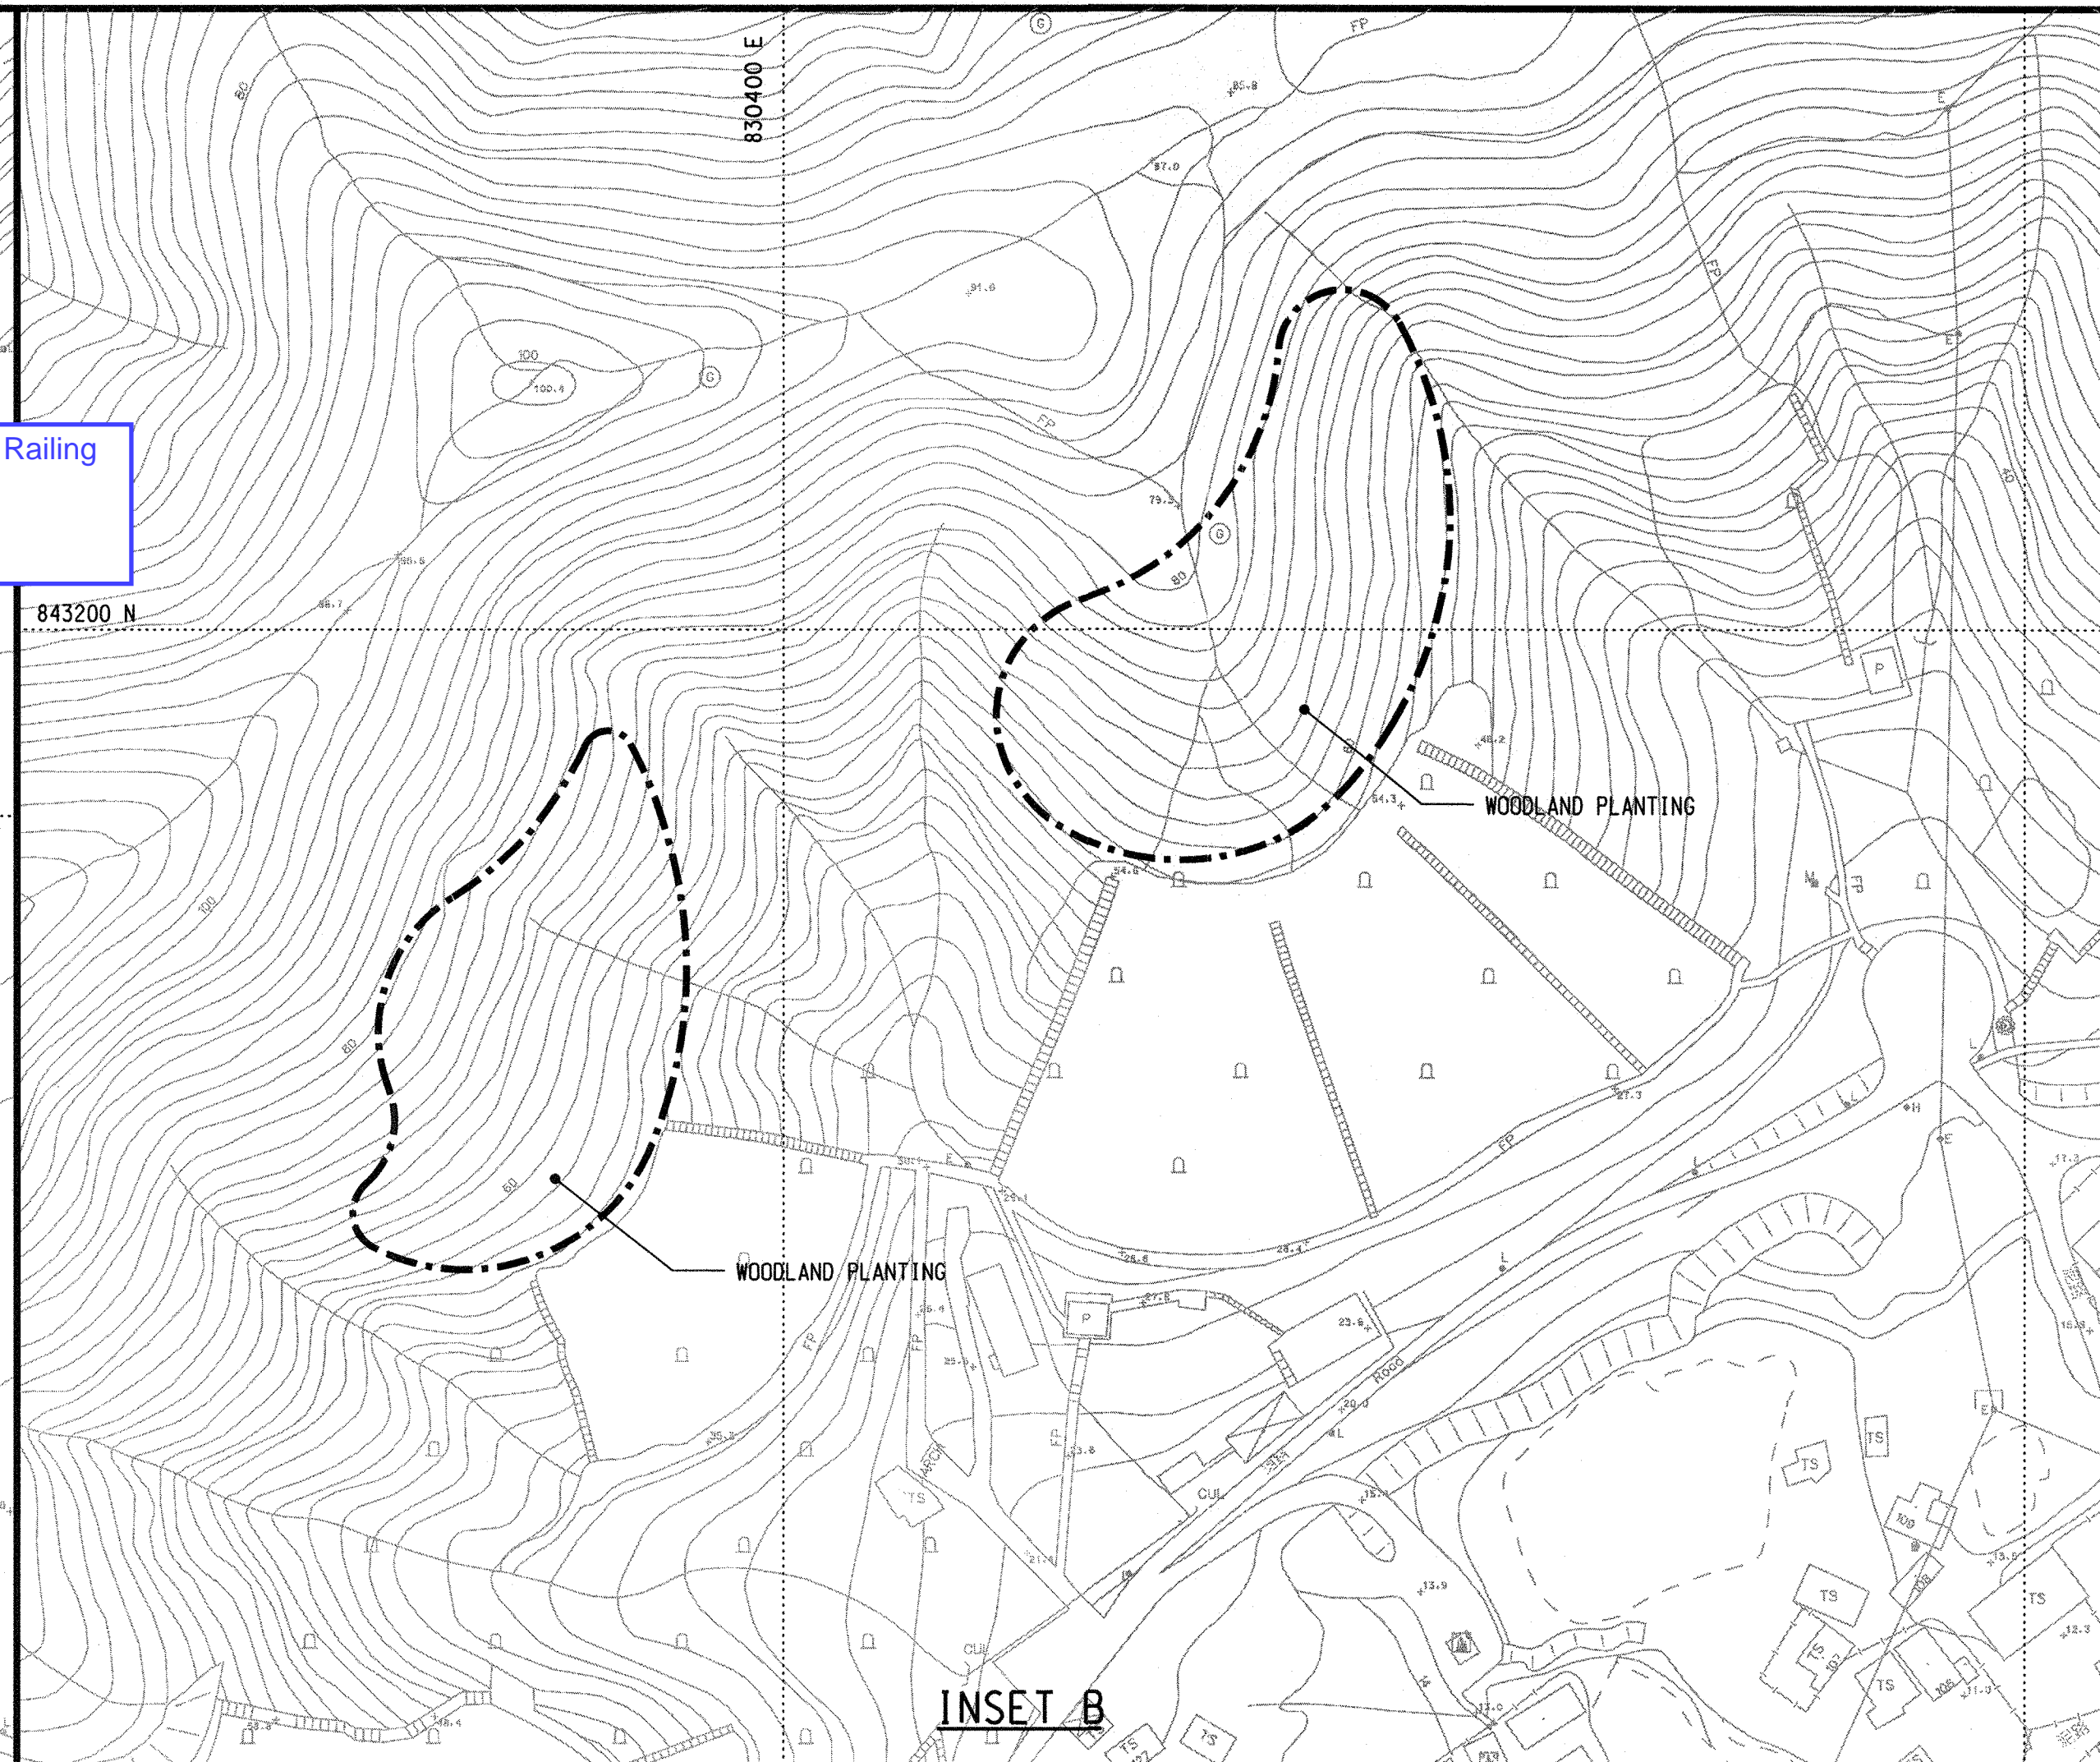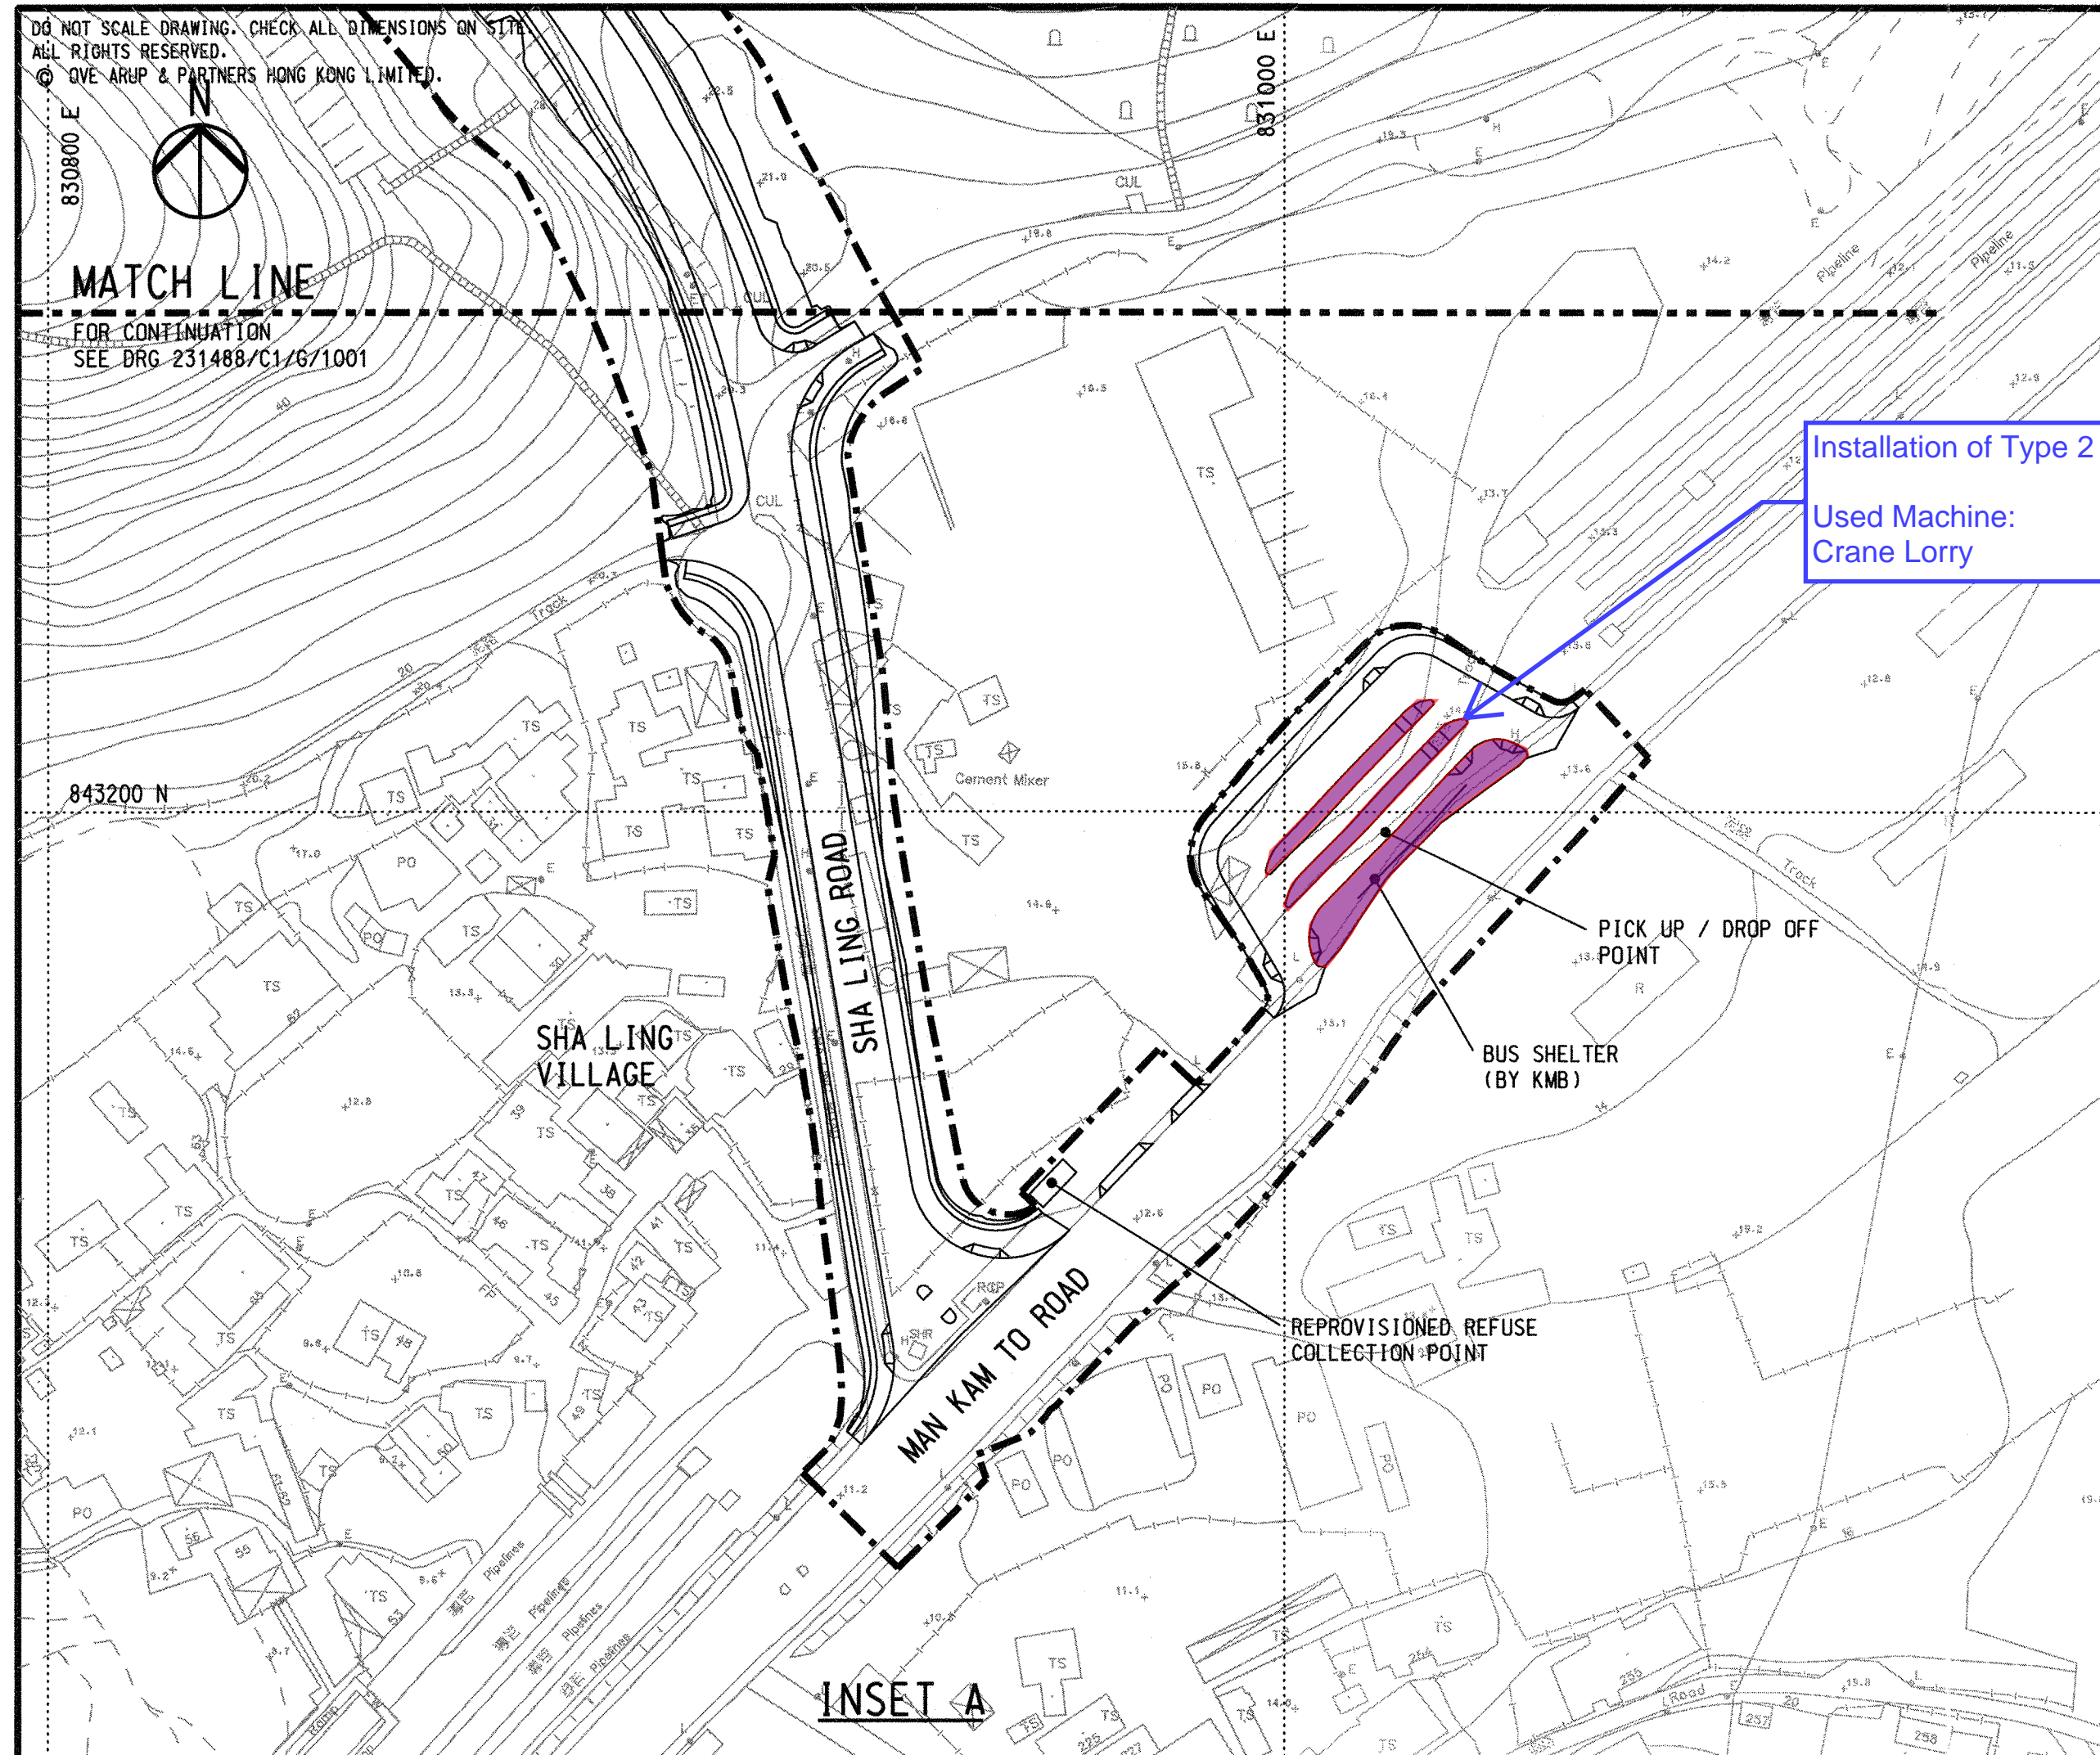

KEY PLAN

LEGEND:  
 - - - - - PROPOSED WORKS SITE

Rev	Description	By	Date

Consultant  
**ARUP**

Contract No. and Title:  
 Contract No. CV/2016/10  
 Site Formation and Associated Infrastructural Works for Development of Columbarium at Sandy Ridge Cemetery

Drawing title  
**GENERAL LAYOUT**  
 (SHEET 2 OF 3)

Drawing no. 231448/C1/G/1002		Rev. -	
Drawn WM	Date 12/16	Checked AW	Approved DL
Scale 1:1000 @A1		Status <b>CONTRACT</b>	



COPYRIGHT RESERVED



土木工程拓展署  
 Civil Engineering and Development Department

Printed by : 11/27/2017  
 Filename : i:\231448\record\contract\civil\231448\_C1\_G\_1002.dgn

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
 ALL RIGHTS RESERVED.  
 © DVE ARUP & PARTNERS HONG KONG LIMITED.

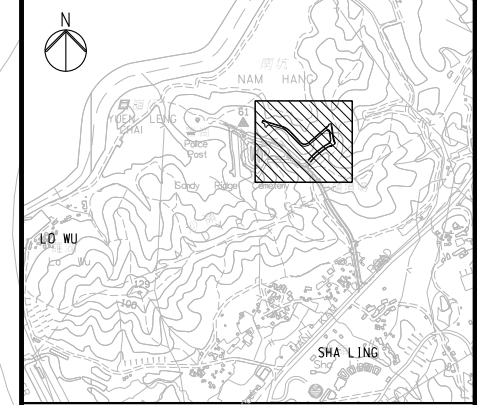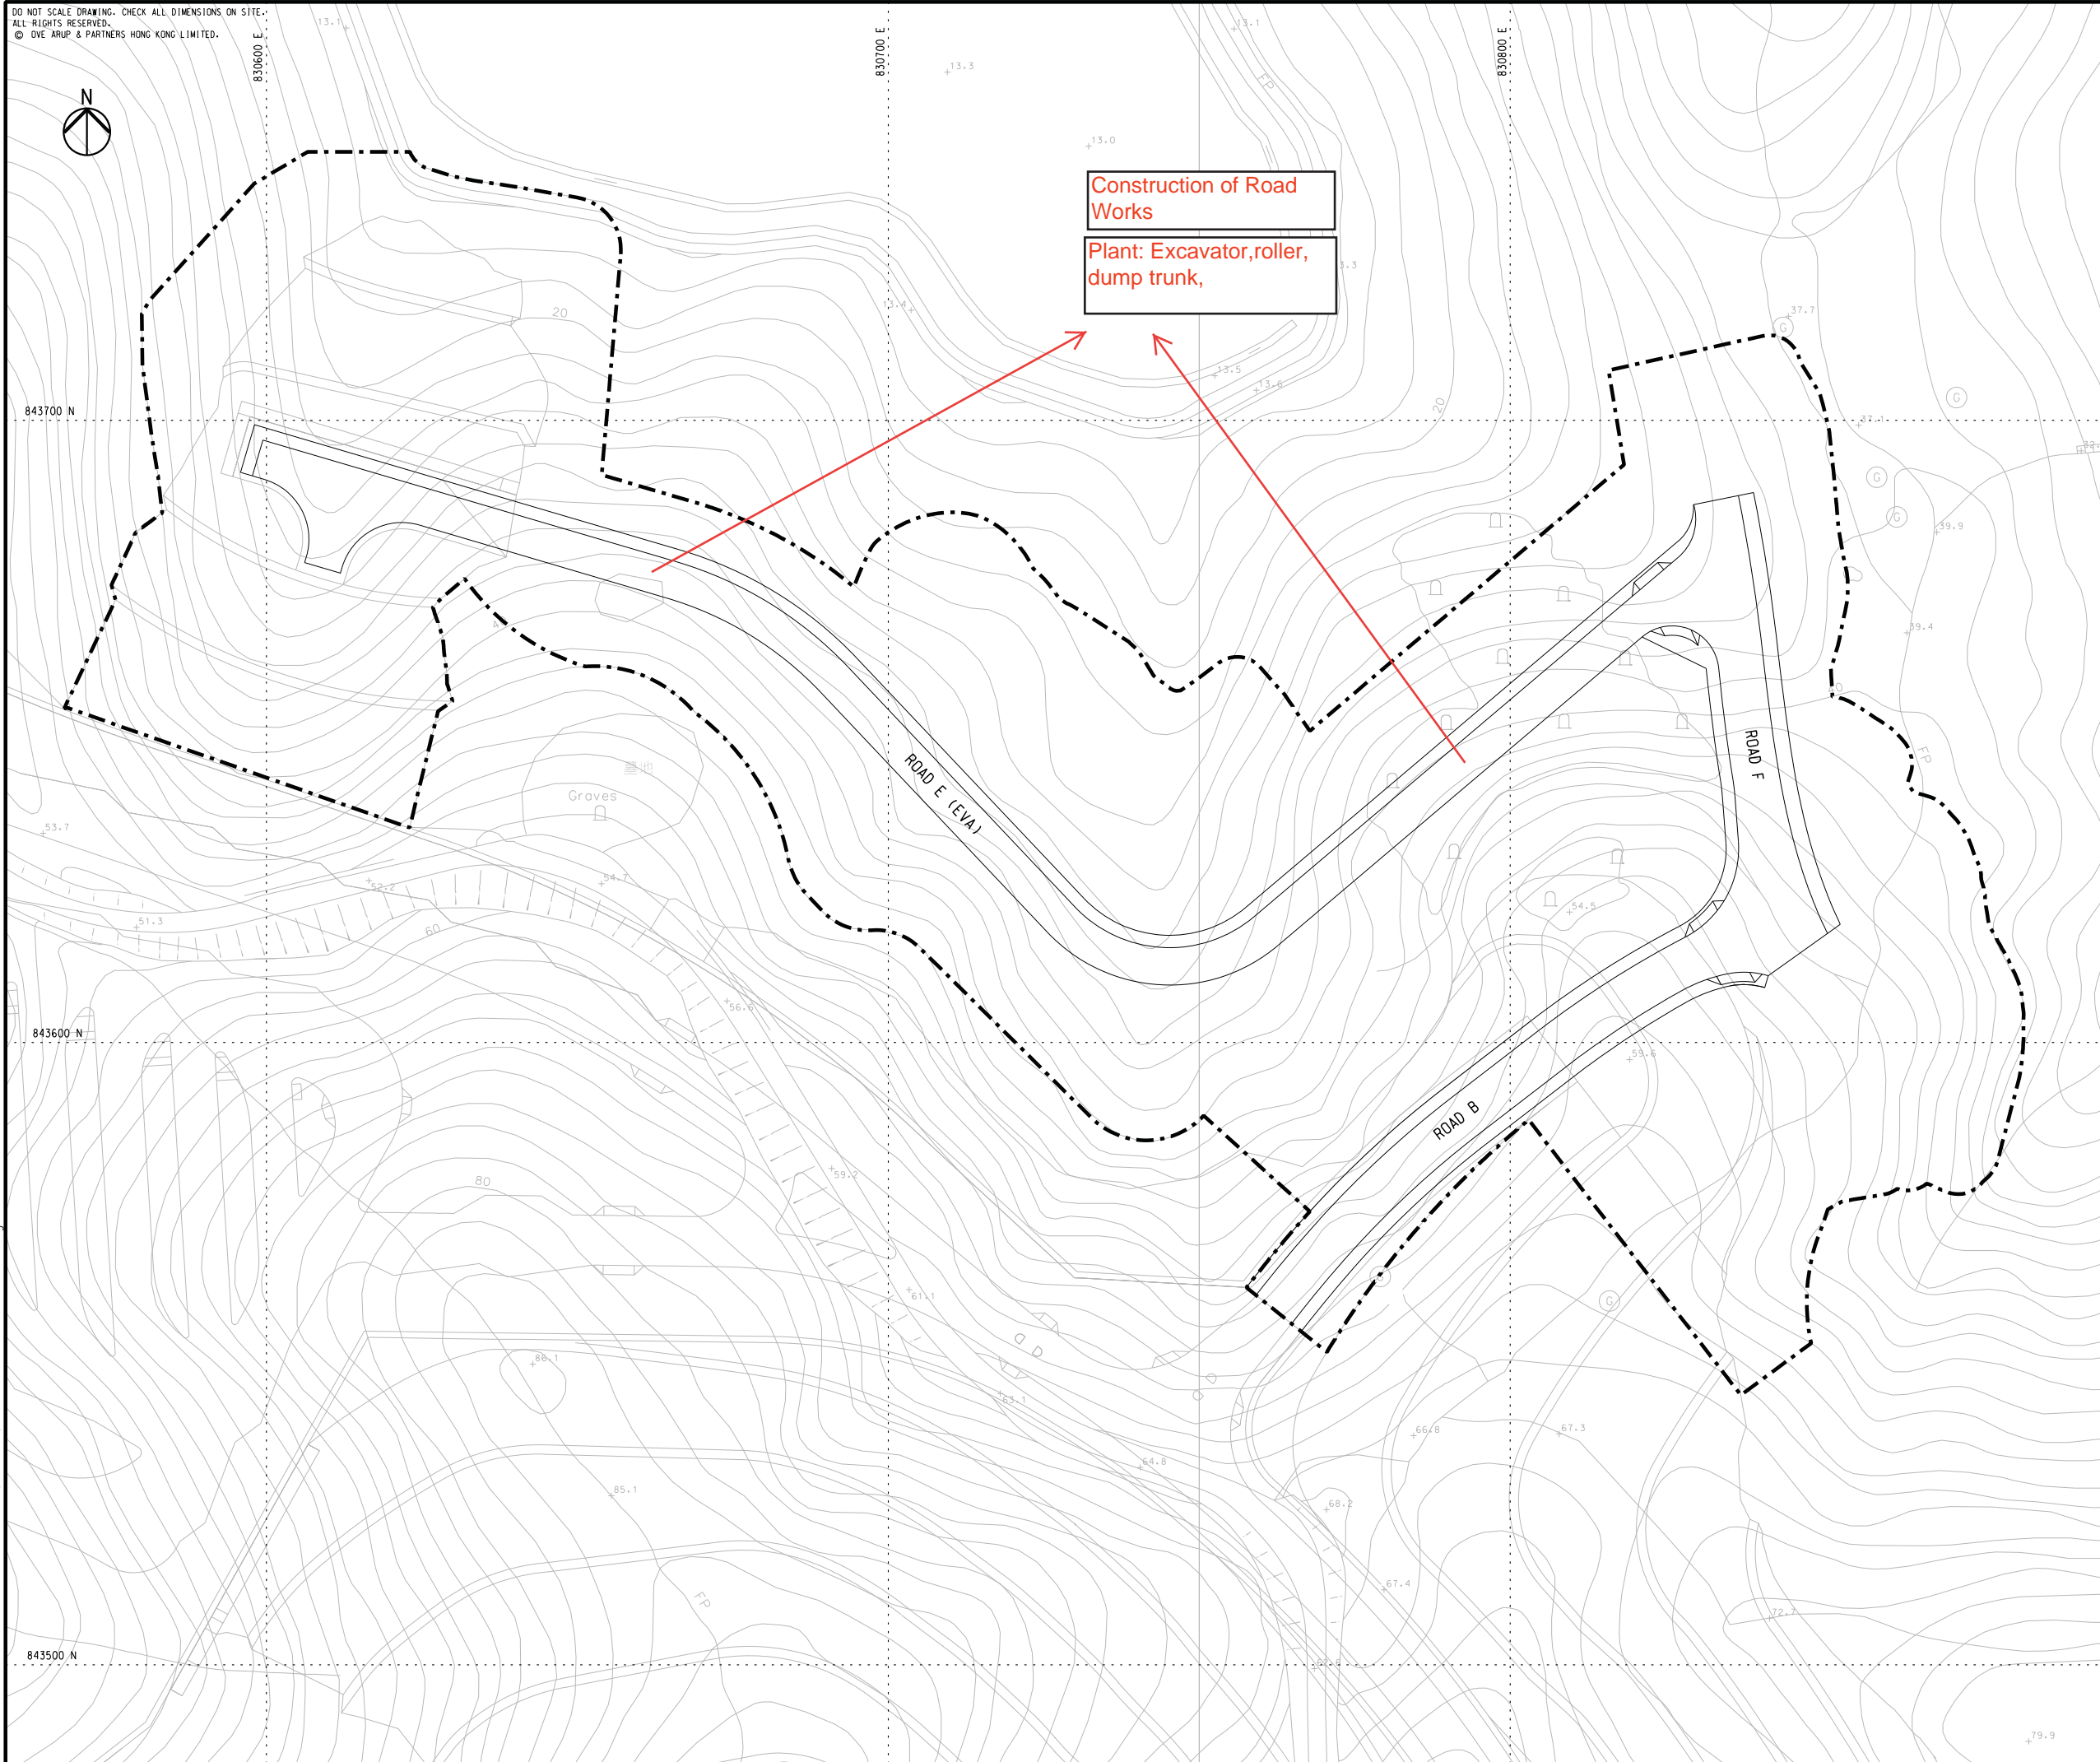

KEY PLAN

LEGEND:

--- SITE BOUNDARY

Rev	Description	By	Date
-	TENDER DRAWING	AW	11/17

Consultant  
**ARUP**

Contract No. and Title:  
 Contract No. CV/2017/02  
 Development of Columbarium  
 at Sandy Ridge Cemetery -  
 Infrastructural Works at  
 Man Kam To Road and  
 Lin Ma Hang Road

Drawing title  
**GENERAL LAYOUT  
 (SHEET 1 OF 5)**

Drawing no. <b>231448/C2/G/1001</b>		Rev. -	
Drawn WM	Date 07/17	Checked AW	Approved DL
Scale 1:500 @A1		Status <b>TENDER</b>	

COPYRIGHT RESERVED



Printed by : 12/27/2017  
 Filename : J:\231448\ARUP\Civil\CONTRACT 2\231448\_C2\_G\_1001.dgn



DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
 ALL RIGHTS RESERVED.  
 © DVE ARUP & PARTNERS HONG KONG LIMITED.

844400 N



844200 N

844000 N


831800 E

832000 E

832200 E

MATCH LINE  
 FOR CONTINUATION SEE  
 DRG. 231448/C2/G/104

Construction of footpath  
 Plant: Excavator, dump truck,

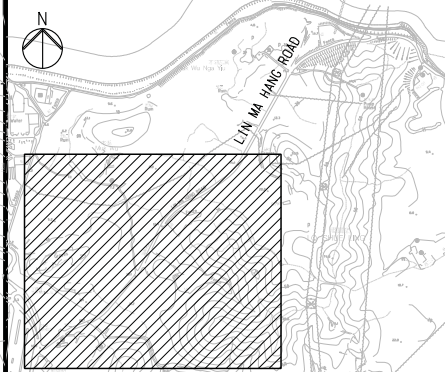

KEY PLAN

NOTE:

- PART(S) OF THE SITE WHICH IS/ARE LOCATED IN THE PUBLIC ROADS AND FOOTPATH SHALL ONLY BE OCCUPIED BY THE CONTRACTOR FOR THE EXECUTION OF THE WORKS WITH PRIOR APPROVAL FROM RELEVANT GOVERNMENT AUTHORITIES INCLUDING ACQUIRING EXCAVATION PERMITS ISSUED BY THE HIGHWAYS DEPARTMENT. THE CONTRACTOR SHALL BE RESPONSIBLE TO ACQUIRE APPROVAL OF HIS TEMPORARY TRAFFIC ARRANGEMENT SCHEMES AND ALL NECESSARY EXCAVATION PERMITS FROM RELEVANT AUTHORITIES.
- THE DEMARCATION AND EXTENT OF THE PART(S) OF THE SITE AS SHOWN ARE APPROXIMATE ONLY AND SHALL BE CONFIRMED ON SITE BY THE PROJECT MANAGER / SUPERVISOR.

LEGEND:

- PART A1
- PART A2
- PART A3
- PART A4
- PART B
- PART C1
- PART C2
- PART D
- PART E

Rev	Description	By	Date
-	TENDER DRAWING	AW	11/17

Consultant  
**ARUP**

Contract No. and Title:  
 Contract No. CV/2017/02  
 Development of Columbarium  
 at Sandy Ridge Cemetery -  
 Infrastructural Works at  
 Man Kam To Road and  
 Lin Ma Hang Road

Drawing title  
**PART OF THE SITE  
 (SHEET 3 OF 5)**


Drawing no. <b>231448/C2/G/1013</b>		Rev. -	
Drawn WM	Date 07/17	Checked AW	Approved DL
Scale 1:1000 @A1		Status <b>TENDER</b>	

COPYRIGHT RESERVED



Printed by : 12/27/2017  
 Filename : J:\231448\ARUP\Civil\CONTRACT 2\231448\_C2\_G\_1013.dgn

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.  
ALL RIGHTS RESERVED.  
©. OVE ARUP & PARTNERS HONG KONG LIMITED.

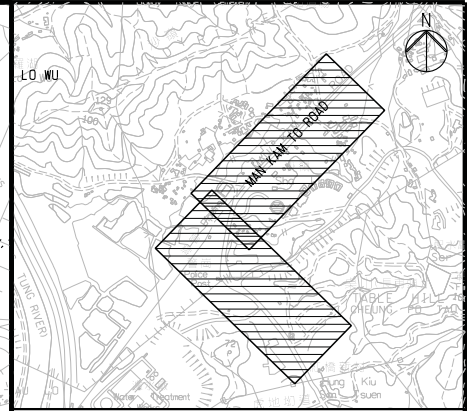


KEY PLAN

- NOTE:**
- PART(S) OF THE SITE WHICH IS/ARE LOCATED IN THE PUBLIC ROADS AND FOOTPATH SHALL ONLY BE OCCUPIED BY THE CONTRACTOR FOR THE EXECUTION OF THE WORKS WITH PRIOR APPROVAL FROM RELEVANT GOVERNMENT AUTHORITIES INCLUDING ACQUIRING EXCAVATION PERMITS ISSUED BY THE HIGHWAYS DEPARTMENT. THE CONTRACTOR SHALL BE RESPONSIBLE TO ACQUIRE APPROVAL OF HIS TEMPORARY TRAFFIC ARRANGEMENT SCHEMES AND ALL NECESSARY EXCAVATION PERMITS FROM RELEVANT AUTHORITIES.
  - THE DEMARCATION AND EXTENT OF THE PART(S) OF THE SITE AS SHOWN ARE APPROXIMATE ONLY AND SHALL BE CONFIRMED ON SITE BY THE PROJECT MANAGER / SUPERVISOR.

**LEGEND:**

	PART A1
	PART A2
	PART A3
	PART A4
	PART B
	PART C1
	PART C2
	PART D
	PART E

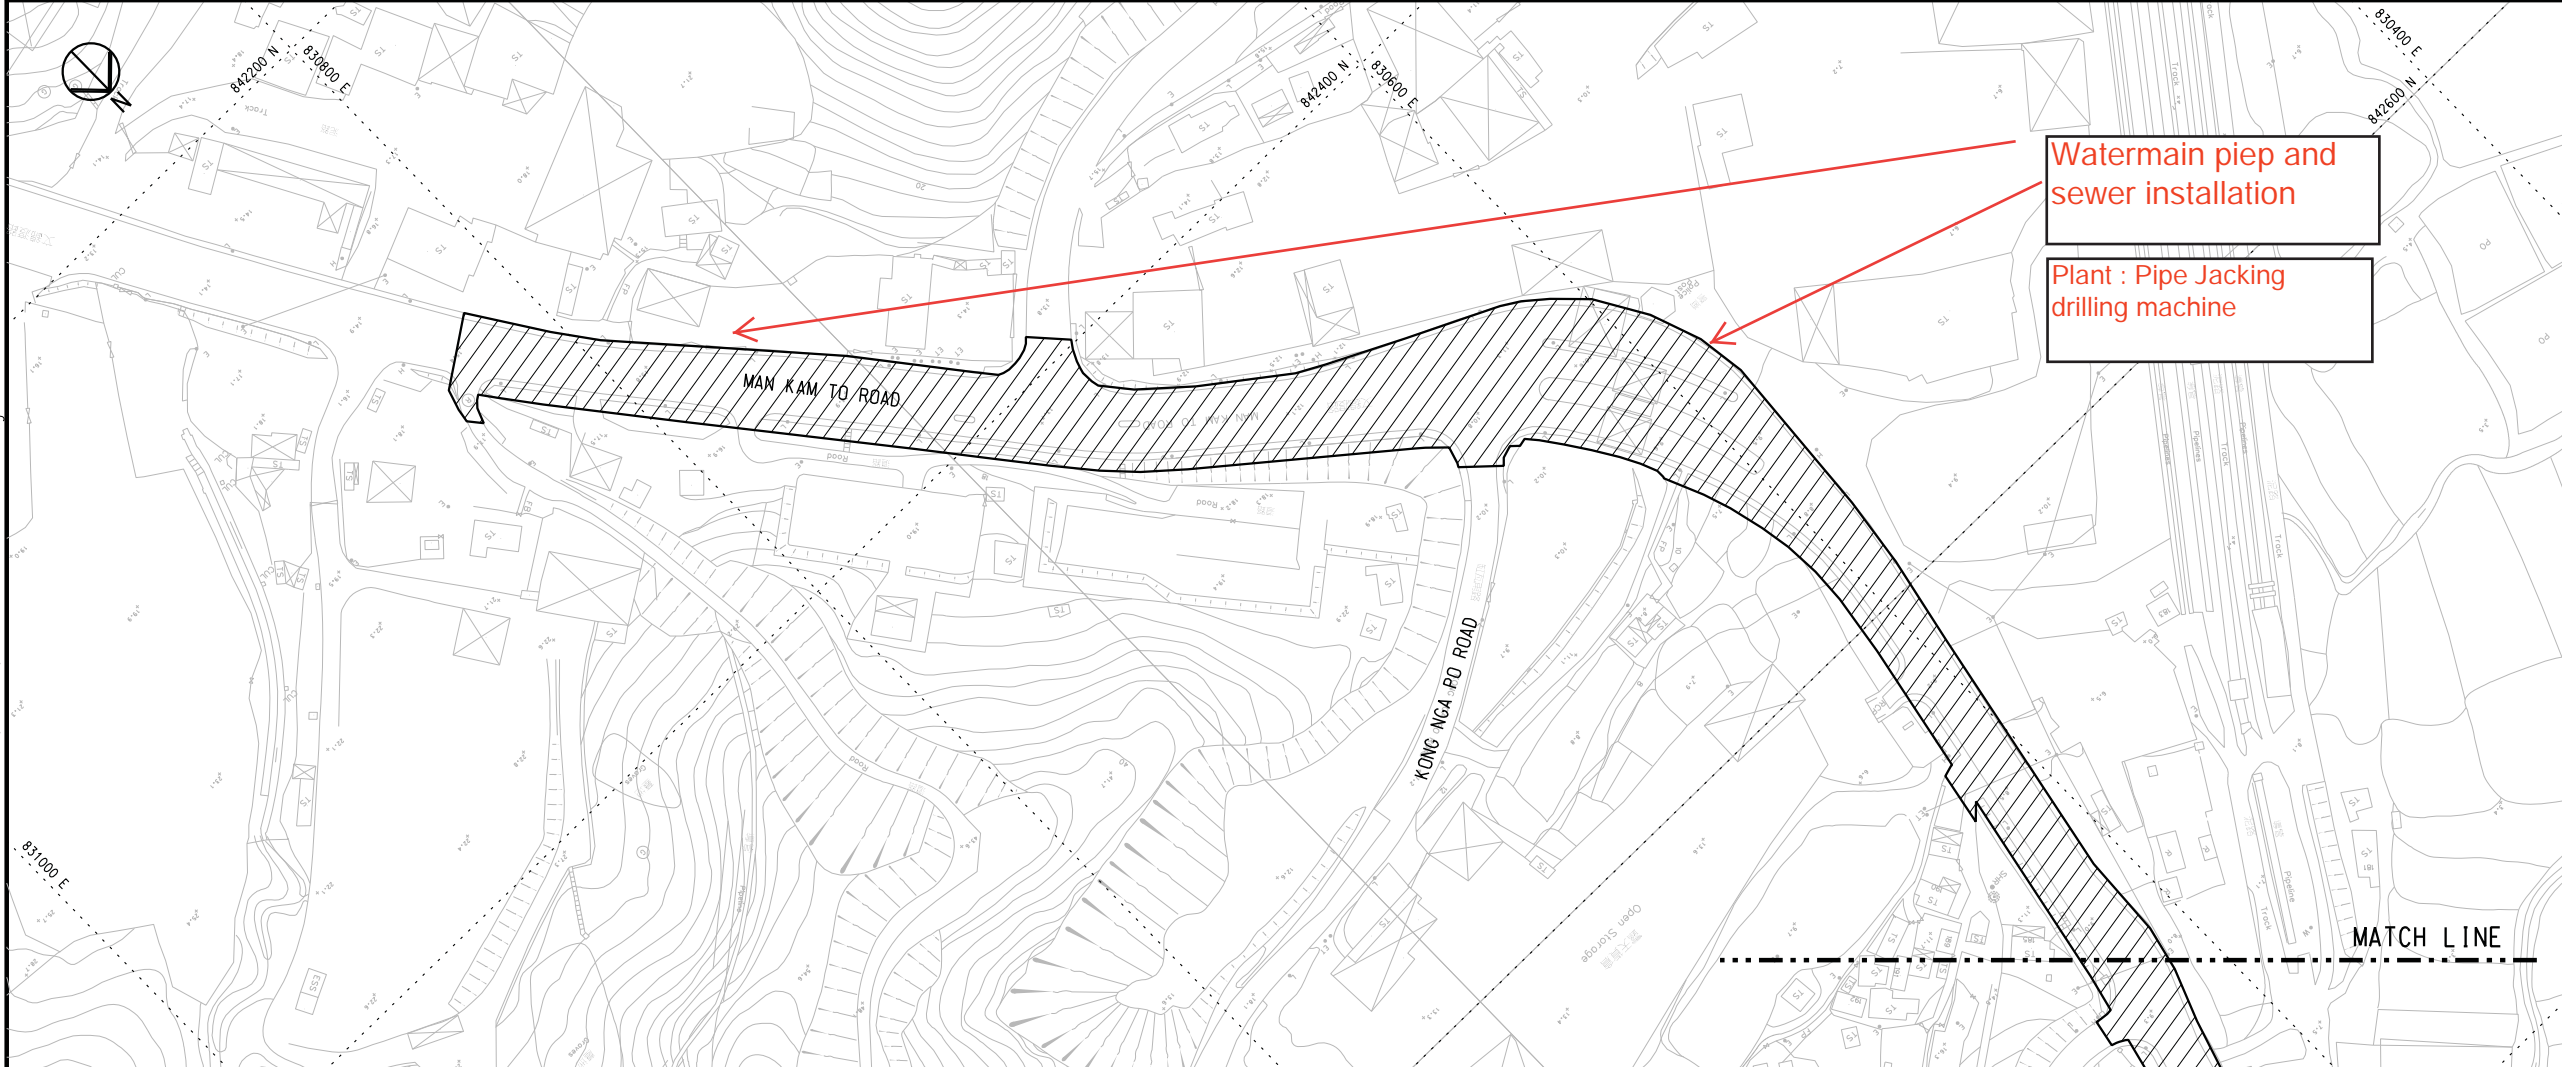

Watermain piep and sewer installation  
Plant : Pipe Jacking drilling machine

-	TENDER DRAWING	AW	11/17
Rev	Description	By	Date

Consultant  
**ARUP**

Contract No. and Title:  
Contract No. CV/2017/02  
Development of Columbarium at Sandy Ridge Cemetery - Infrastructural Works at Man Kam To Road and Lin Ma Hang Road

Drawing title  
**PART OF THE SITE (SHEET 2 OF 5)**

Drawing no. <b>231448/C2/G/1012</b>		Rev. -	
Drawn WM	Date 07/17	Checked AW	Approved DL
Scale 1:1000 @A1		Status <b>TENDER</b>	

Copyright Reserved

土木工程拓展署  
Civil Engineering and Development Department

Printed by : 12/27/2017  
Filename : J:\231448\ARUP\Civil\CONTRACT 2\231448\_C2\_G\_1012.dgn
