
Vol. 3 of 5 FEP-03/457/2013/D Central Kowloon Route Yau Ma Tei East Contract No. HY/2014/08 November 2022





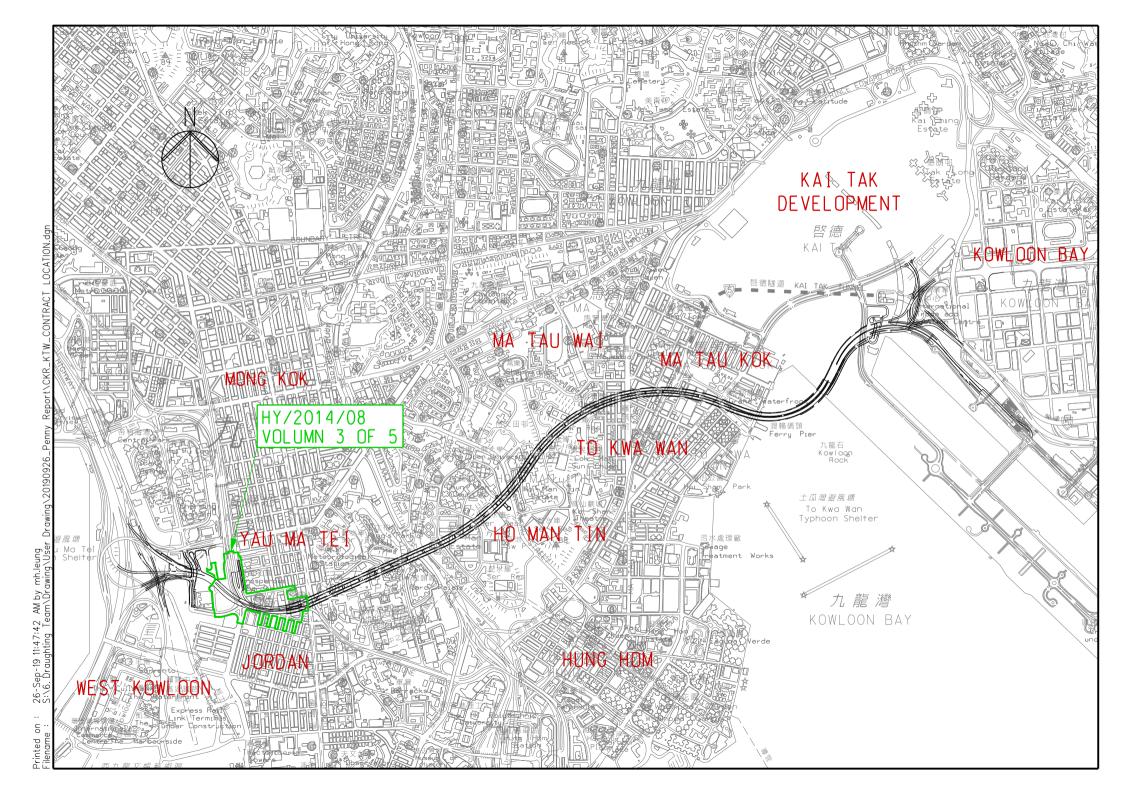

Environmental Permit No. EP-457/2013/D

Central Kowloon Route

Independent Environmental Checker Verification

Yau Ma Tei Fast (HY/2014/08)

· · · · · · · · · · · · · · · · · · ·	144 1/14 101 2400 (111/2014 00)
Reference Document/Plan	
Document/ Plan to be Certified / Verified:	Monthly EM&A Report No.56 (December 2022)
Date of Report:	8 December 2022 (Rev.1)
Date received by IEC:	9 December 2022

Reference EP Condition

Works Contract

Environmental Permit Condition: 3.4

Submission of Monthly EM&A Report of the Project

3.4 Four hard copies and one electronic copy of monthly EM&A Report shall be submitted to the Director within 2 weeks after the end of each reporting month throughout the entire construction period. The EM&A Reports shall include a summary of all non-compliance. The submissions shall be certified by the ET Leader and verified by the IEC as complying with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of the submission shall be provided to the Director upon request by the Director.

IEC Verification

I hereby verify that the above referenced document/plan complies with the above referenced condition of EP-457/2013/D.

Ms Mandy To

Mondy 20.

Date:

9 December 2022

Independent Environmental Checker

Our ref: 0436942_IEC Verification Cert_YMTE_Monthly EM&A Rpt No.56.docx





Build King – SK ecoplant Joint Venture

Central Kowloon Route Contract HY/2014/08 Section of Yau Ma Tei East

Monthly EM&A Report No. 56

(Period from 1 to 30 November 2022)

Rev. 1

(8 December 2022)

	Name	Signature
Prepared by	Janice K.C. Lee (Environmental Consultant)	J
Checked & Reviewed by	Y.H. Law (Senior Environmental Consultant)	Malai
Approved & Certified by	Kevin W. M. Li (Environmental Team Leader)	K;

TABLE OF CONTENTS

EXECUTIVE SUMMARY

1.	BASIC PROJECT INFORMATION	7
2.	ENVIRONMENTAL STATUS	11
3.	MONITORING RESULTS	13
4.	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS	21
5.	EM&A SITE INSPECTION	23
6.	FUTURE KEY ISSUES	24
7.	CONCLUSION AND RECOMMENDATIONS	25

LIST OF APPENDICES

- A. Alignment and Works Area for the Contract No. HY/2014/08
- B. Construction Programme
- C. Project Organization Chart
- D. Dust Event-Action Plan (EAP)
- E. Noise Event-Action Plan (EAP)
- F. Environmental Mitigation Implementation Schedule (EMIS)
- G. Monitoring Schedules of the Reporting Month
- H. Calibration Certificate (Air Monitoring)
- I. Calibration Certificate (Noise)
- J. The Certification of Laboratory with HOKLAS Accredited Analytical Tests
- K. Location Plan of Noise and Air Quality Monitoring Station
- L. Monitoring Data (Air Monitoring)
- M. Monitoring Data (Noise)
- N. Waste Flow Table
- O. Statistics on Complaint, Notifications of Summons and Successful Prosecutions
- P. Monitoring Schedule of the Coming Month
- Q. Interim Report for the Complaint

EXECUTIVE SUMMARY

- A.1 Build King SK ecoplant Joint Venture ("Contractor") commenced the construction works of Highway Department (HyD) Central Kowloon Route Contract No. HY/2014/08 Section of Yau Ma Tei East ("The Project") on 20 April 2018. This is the 56th monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A works carried out during the period from 1 November 2022 to 30 November 2022.
- A.2 A summary of the construction works reported by Main Contractor for the Project during the reporting month is listed below.

Construction Activities undertaken

- Construct D-wall panels, pumping test, excavation to roof slab & construct roof slab at Zone B
- Install Underground Utilities hanger support, excavation to roof slab and construct roof slab at Zone B
- Install Underground Utilities hanger support, excavation to roof slab and construct roof slab at Zone C
- Install Underground Utilities hanger support, excavation to roof slab and construct roof slab at Zone D
- Underground Utilities diversions, CLP Cable Tunnel A demolition, Jet Grouting, Pre-boring, Dwall construction, install kingposts/recharge well/observation well/pumping well and Pumping Test at Zone F
- Underground Utilities diversion, Jet Grouting, Preboring, Pipe Piles / D-wall construction, install king posts/ recharge well/observation well/pumping well and Pumping Test at Zone G
- Construct portal frame across, demolish existing Gascogine Road Flyover beams and construct end span at Portion 21
- Construct bridge deck for spans P2 to P6 at Gascogine Road Flyover
- Construct socketed H-piles, pile caps, ground beams, reinforced concrete columns and erect steel posts of Noise Enclosure at Zone 3
- Underground Utilities diversion, construct permanent & temporary pipe piles, barrette walls for Noise Enclosure at Zone 2
- A.3 A summary of regular construction noise and construction dust monitoring activities in this reporting period is listed below:

Regular construction noise monitoring during normal working hours

W-N1A, W-P11, W-N18, W-N25A 6 times

Construction dust (24-hour TSP) monitoring

W-A1 6 times W-A6 6 times

Construction dust (1-hour TSP) monitoring

W-A1, W-A6 18 times

A.4 Bi-weekly inspection of the implementation of landscape and visual mitigation measures was conducted on 10 and 24 November 2022. Details of the audit findings and implementation status are presented in Section 5.

- A.5 Joint weekly site inspections were conducted by representatives of Environmental Team (ET), Contractor and Engineer on 3, 10, 17 and 24 November 2022. One joint site inspection with IEC was also undertaken on 10 November 2022. Details of the audit findings and implementation status are presented in Section 5.
- A.6 Details of waste management are presented in Section 3.
- A.7 Four Action Levels of construction noise were triggered during the reporting month as documented complaints related to construction noise from works areas at Zone 3 Noise Enclosure and Zone D3, whereas two complaints were received on 11 November 2022, two complaints were received on 14 November 2022 and 17 November 2022 respectively. No exceedance of Limit Level of construction noise was recorded in the reporting month. No exceedance of the Action and Limit Level of 24-hour TSP and 1-hour TSP was recorded in the reporting month.
- A.8 Four noise related complaints were received in the reporting month, whereas two complaints were received on 11 November 2022, two complaints were received on 14 November 2022 and 17 November 2022 respectively. Two complaints were concluded as non-project related. After investigation with Contractor, precautionary measures had been proposed to the Contractor by ET. The interim report for the complaint is shown in Appendix Q.
- A.9 No non-compliance was reported in the reporting month.
- A.10 No notification of summon or prosecution was received in this reporting month.
- A.11 A summary of the construction activities provided by Main Contractor in the next reporting month is listed below:

Construction Activities to be undertaken

- Removal of Struts and construction of Lower Ventilation Duct Columns at Zone A
- Installation of Underground Utilities Hanger Support, exposure of box culvert and plugging of abandoned pipe at Zone B
- Install hanger support for existing Underground Utilities under traffic deck, excavation to roof slab in Zone B, C and D
- Construction of ceiling slab at Zone B1
- Underground Utilities diversion and D-wall construction at Zone B3
- Underground Utilities diversion, jet grouting, pre-boring works and D-wall construction at Zone F
- DN1800 drainage diversion work and ground improvement at Dickson/Tak Cheong Buildings (TAM Grouting, jet grouting) works at Zone G
- Works for reprovisioning of Gascogine Road Flyover at HKAA area: Falsework erection and end span construction for P7L
- Bridge Works:
 - i. FT1- bridge deck construction for P3L
 - ii. FT2- bridge deck construction for P2L
- Temporary parapet and noise barriers construction for P4L to P6L

Construction Activities to be undertaken

- Complete remaining socketted H-pile works for middle and west side of F02 Noise Enclosure in Zone 3, continue excavation and lateral support and construction works for pile caps and ground beams construction for middle / east foundation for F02 Noise Enclosure
- Erection of Y columns, side columns and main beams for Noise Enclosure F02 in Zone 3 (night works)
- Works at Zone 2 Noise Enclosure scheduled as the following:
 - i. Column E & A Excavation and Lateral Support works and pile cap construction
 - ii. Column G Permanent diversion of uncharted drainage pipe
 - iii. Columns A1 Construct temporary reinforced concrete pile cap and erect steel tower
 - iv. Column C Complete design and fabrication of steel footing and install steel footing
 - v. Columns D Temporary socketted H-pile works
- Noise Enclosure steelworks fabrication at Fabrication Yard in Zhuhai, China
- Monitoring of instrumentation for all areas

1. Basic Project Information

- 1.1. Central Kowloon Route (CKR) is a 4.7 km long dual 3-lane trunk road in Central Kowloon linking Yau Ma Tei Interchange in West Kowloon with the road network on Kai Tak Development and Kowloon Bay in East Kowloon.
- 1.2. The Central Kowloon Route Design and Construction Environmental Impact Assessment Report (Register No.: AEIAR-171/2013) was approved with conditions by the Environmental Protection Department (EPD) on 11 July 2013. An Environmental Permit (EP 457/2013) was issued on 9 August 2013. Variations of EP (VEP) was applied for and the EP (EP-457/2013/C) was issued by EPD on 16 January 2017. Variations of EP (VEP) was subsequently applied for and the latest EP (EP-457/2013/D) was issued by EPD on 15 June 2021. A Further EP (FEP-03/457/2013/D) was issued by EPD on 5 November 2021.
- 1.3. The construction of the CKR had been divided into different sections. This Contract No. HY/2014/08 Section of Yau Ma Tei East (YMTE) covers part of the construction activities located at Yau Ma Tei under the EP and FEP which includes:
 - Section of Yau Ma Tei East
 - i. Construction of Cut-and-Cover Tunnel in compliance with all statutory requirements and the requirements specified under the Contract while maintaining the traffic with all necessary provisions
 - ii. Construction and subsequent handover of Yau Ma Tei Access Shaft for facilitating the access and use by the contractor of Central Kowloon Route Central Tunnel contract
 - iii. Demolition of existing buildings including Yau Ma Tei Multi-storey Carpark Building, Yau Ma Tei Specialist Clinic Extension Building and Yau Ma Tei Jade Hawker Bazaars
 - iv. Demolition and re-provisioning of Gascoigne Road Flyover and the underpinning works for the existing Ferry Street Flyover and Yau Ma Tei Police Station New Wing Building
 - v. Construction of civil provisions and coordination with the contractor of Central Kowloon Route Tunnel Electrical & Mechanical contract
 - vi. Design and construction of Noise Barrier Works
 - vii. Prepare temporary traffic arrangement proposals, discuss at Traffic Management Liaison Group meeting and obtain its agreement and approval/endorsement from relevant authorities at suitable times to enable the execution of the Works

The alignment and works area for the Contract No. HY/2014/08 - are shown in Appendix A.

1.4. A summary of the major construction activities undertaken in this reporting period is shown in Table 1.1. The construction programme is presented in Appendix B.

Table 1.1 Summary of the Construction Activities reported by Main Contractor during the Reporting Month

Construction Activities undertaken

- Construct D-wall panels, pumping test, excavation to roof slab & construct roof slab at Zone B
- Install Underground Utilities hanger support, excavation to roof slab and construct roof slab at Zone B
- Install Underground Utilities hanger support, excavation to roof slab and construct roof slab at Zone C
- Install Underground Utilities hanger support, excavation to roof slab and construct roof slab at Zone D
- Underground Utilities diversions, CLP Cable Tunnel A demolition, Jet Grouting, Pre-boring, Dwall construction, install kingposts/recharge well/observation well/pumping well and Pumping Test at Zone F
- Underground Utilities diversion, Jet Grouting, Preboring, Pipe Piles / D-wall construction, install king posts/ recharge well/observation well/pumping well and Pumping Test at Zone G
- Construct portal frame across, demolish existing Gascogine Road Flyover beams and construct end span at Portion 21
- Construct bridge deck for spans P2 to P6 at Gascogine Road Flyover
- Construct socketed H-piles, pile caps, ground beams, reinforced concrete columns and erect steel posts of Noise Enclosure at Zone 3
- Underground Utilities diversion, construct permanent & temporary pipe piles, barrette walls for Noise Enclosure at Zone 2
 - 1.5. The project organisational chart specifying management structure and contact details are shown in Appendix C.
 - 1.6. A summary of the valid permits, licences, and /or notifications on environmental protection for this Project is presented in Table 1.2.

Table 1.2 Summary of the Status of Valid Environmental Licence

Notification, Permit and Documentations

Permit/ Licences/	Valid	Period		
Notification /Reference No.	From	То	Status	Remark
Environmental Permit				
EP-457/2013/D	15 Jun 2021	End of Project	Valid	-
Further Environmental l	Permit			
FEP-03/457/2013/D	5 Nov 2021	End of Project	Valid	
Wastewater Discharge Li	cense			
WT00030660-2018	28 Mar 2018	31 Mar 2023	Valid	-
Notification of Constructi	ion Works under	the Air Pollution	n Control (Construction	n Dust) Regulation
471691	14 Sep 2021	End of Project	Notified	-
Chemical Waste Produce	Chemical Waste Producer Registration			
WPN5213-225-B2526-01	14 Mar 2018	End of Project	Valid	-
Billing Account for Disposal of Construction Waste				
7029997	1 Feb 2018	End of Project	Valid	-
Construction Noise Permit				

Permit/ Licences/ Valid Period				
Notification /Reference No.	From	То	Status	Remark
GW-RE0492-22	20 May 2022	19 Nov 2022	CNP renewal is under application	Construction Noise Permit at P6
GW-RE0529-22	31 May 2022	26 Nov 2022	Supersede by GW-RE1124-22	Construction Noise
GW-RE1124-22	22 Oct 2022	19 Apr 2023	Valid	Permit at Zone A & B1
GW-RE0716-22	15 Jul 2022	14 Jan 2023	Valid	Construction Noise Permit at Zone 3
GW-RE0804-22	12 Aug 2022	11 Nov 2022	Supersede by GW-RE1210-22	Construction Noise
GW-RE1210-22	12 Nov 2022	11 Feb 2023	Valid	Permit at Zone D & P3
GW-RE1009-22	6 Oct 2022	30 Nov 2022	CNP renewal is under application	Construction Noise Permit for disassembly, assembly and lanching of Form Traveller at Kansu Street between Shanghai Street and Canton Road
GW-RE1015-22	6 Oct 2022	31 Dec 2022	Valid	Construction Noise Permit for Inspection and Maintenance (Road Resurfacing)
GW-RE1017-22	1 Oct 2022	31 Dec 2022	Valid	Construction Noise Permit for Erection of Enclosure at Zone 3
GW-RE1109-22	20 Oct 2022	30 Nov 2022	CNP renewal is under application	Construction Noise Permit at GRF for Temporary Erection of Bridge Decking
GW-RE1111-22	21 Oct 2022	19 Jan 2023	Valid	Construction Noise Permit at Zone B3 & F
GW-RE1116-22	21 Oct 2022	20 Jan 2023	Valid	Construction Noise Permit at Zone B2 & C
GW-RE1148-22	1 Nov 2022	31 Dec 2022	Valid	Construction Noise Permit at P2
GW-RE1223-22	18 Nov 2022	31 Dec 2022	Valid	Construction Noise Permit for Central Divider Removal at GRF

Permit/ Licences/ Notification /Reference No. Marine Dumping Permit	Valid Period		Status	Remark
EP/MD/23-016	23 Jun 2022	22 Dec 2022	Valid	Type 1 – Open Sea Disposal
EP/MD/23-049	25 Oct 2022	24 Nov 2022	Supersede by ER/MD/23-062	Dumping at Sea Permit (Type 1 – Open Sea Disposal (Dedicated
ER/MD/23-062	25 Nov 2022	24 Dec 2022	Valid	Site) & Type 2 - Confined Marine Disposal)

2. ENVIRONMENTAL STATUS

2.1. Environmental permit (EP) conditions under the EIAO, submission status under the EP and implementation status of mitigation measures had been reviewed and implemented on schedule. The status of required submissions under the EP (EP-457/2013/D) and FEP (FEP-03/457/2013/D) as of the reporting period for the Project are summarised in Table 2.1

Table 2.1 Summary of Status of Required Submission for EP-457/2013/D and FEP-03/457/2013/D for the Project

EP/FEP Condition (EP-457/2013/D) (FEP-03/457/2013/D)	Submission	Submission date
Condition 3.4	Monthly EM&A Report (Oct 2022)	14 Nov 2022

2.2. Details of the major construction activities reported by Main Contractor in this reporting period are shown in Table 2.2.

Table 2.2 Summary of the Construction Activities reported by Main Contractor during the Reporting Month

Construction activities undertaken	Remarks on progress
 Construct D-wall panels, pumping test, excavation to roof slab & construct roof slab at Zone B 	• 93% completion
 Install Underground Utilities hanger support, excavation to roof slab and construct roof slab at Zone B 	• 20% completion
• Install Underground Utilities hanger support, excavation to roof slab and construct roof slab at Zone C	• 22% completion
• Install Underground Utilities hanger support, excavation to roof slab and construct roof slab at Zone D	• 22% completion
 Underground Utilities diversions, CLP Cable Tunnel A demolition, Jet Grouting, Pre-boring, D-wall construction, install kingposts/ recharge well/observation well/pumping well and Pumping Test at Zone F 	• 37% completion
 Underground Utilities diversion, Jet Grouting, Preboring, Pipe Piles / D-wall construction, install king posts/ recharge well/observation well/pumping well and Pumping Test at Zone G 	• 35% completion
 Construct portal frame across, demolish existing Gascoigne Road flyover beams and construct end span at Portion 21 	• 92% completion
Construct bridge deck for spans P2 to P6 at Gascoigne Road flyover	• 72% completion
 Construct socketed H-piles, pile caps, ground beams, reinforced concrete columns and erect steel posts of Noise Enclosure at Zone 3 	• 73% completion
 Underground Utilities diversion, construct permanent & temporary pipe piles, barrette walls for Noise Enclosure at Zone 2 	• 61% completion

2.3. The drawing showing the project layout and the location of the monitoring station and environmental sensitive receivers are attached in Appendix A and Appendix K. Co-ordinates of the monitoring location are shown in Table 2.3.

Table 2.3 Summary for the location of the monitoring station

Monitoring Location	Location ID	Latitude	Longitude
Yau Ma Tei Catholic Primary School (Hoi Wang Road)*	W-A1/ W-N1A	22.31345	114.16409
Man Cheong Building	W-A6	22.308185	114.166033
Hydan Place	W-N18	22.30858	114.170185
Prosperous Garden Block 1	W-N25A	22.309846	114.168072
The Coronation Tower 1	W-P11	22.309824	114.165616

Remark: *The High Volume Sampler (HVS) at dust impact monitoring location W-A1 had been relocated on 6 Sep 2022 due to installation work of PV panel at Yau Ma Tei Catholic Primary School. The relocation of HVS was approved by ER and agreed with IEC.

3. MONITORING RESULTS

3.1. Monitoring Parameters

Air Quality

- 3.1.1. The impact monitoring had been carried out in accordance with section 5.8 of the approved EM&A Manual to determine the 1-hour and 24-hour total suspended particulates (TSP) levels at the monitoring locations in the reporting month.
- 3.1.2. The sampling frequency of at least once in every 6 days, shall be strictly observed at the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least 3 times in every 6 days should be undertaken when the highest dust impact occurs.
- 3.1.3. General meteorological conditions (wind speed, direction and precipitation) and notes regarding any significant adjacent dust producing sources had also been recorded throughout the impact monitoring period.

Noise

- 3.1.4. Construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). Leq (30min) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays.
- 3.1.5. For all other time periods, Leq (5min) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria.
- 3.1.6. As supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.
- 3.2. Monitoring Equipment

Air Quality

- 3.2.1. 1-hour TSP levels and 24-hour TSP had been measured with direct reading dust meter and High Volume Samplers respectively. It has been demonstrated its capability in achieving comparable results with high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50).
- 3.2.2. The 1-hour TSP meter was calibrated by the manufacturer prior to purchasing. Zero response of the instrument was checked before and after each monitoring event. Operation of the 1-hour TSP meter followed manufacturer's Operation and Service Manual. The 24-hour TSP meter was calibrated against firmware 80570-8100-V1.0.4, annually. Operation of the 24-hour TSP meter followed manufacturer's Operation and Service Manual. Valid calibration certificates of dust monitoring equipment are attached in Appendix H.
- 3.2.3. A summary of the equipment that was deployed for the 24- hour averaged monitoring is shown in Table 3.1. The TSP monitoring was conducted as per the schedule presented in Appendix G.

3.2.4. The equipment used for 1-hour TSP and 24-hour TSP measurement and calibration are summarised in Table 3.1

\mathcal{E} 1 1			
Monitoring Parameter	Monitoring Equipment	Serial Number	Date of Calibration
	LD-5R Digital Dust Indicator	0Z4545	3 Apr 2022
1-hour TSP	LD-5R Digital Dust Indicator	992820	3 Apr 2022
1-Hour 1SP	PC-3A(E) Digital Dust Indicator	JC2002224	3 Apr 2022
	PC-3A(E) Digital Dust Indicator	JC2002225	3 Apr 2022
	TE-5170X High Volume	1084	1 Nov 2022 and 16
	Sampler		Nov 2022
24-hour TSP	TE-5170X High Volume	1050	1 Nov 2022 and 16
	Sampler		Nov 2022
	TE-5025A Calibration Kit	3465	28 Jun 2022

Table 3.1 Construction Dust Monitoring Equipment

Noise

- 3.2.5. Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications has been used for carrying out the noise monitoring. The sound level meter has been checked using an acoustic calibrator. The wind speed and other metrological data has been recorded from Hong Kong Observatory- King's Park meteorological station, along with portable wind speed meter stand by as back up when the information are not available from HKO.
- 3.2.6. Acoustic calibrators and sound level meters using for the monitoring is within the valid period and were calibrated per year. Valid calibration certificate of noise monitoring equipment is attached in Appendix I.
- 3.2.7. The details of equipment using for monitoring are listed in Table 3.2, as below:

	\mathcal{E} 1 1	C
Monitoring Equipment	Serial Number	Date of Calibration
Nti XL2 Sound Level Meter	A2A-13548-E0	3 Jan 2022
Lutron SL-4033SD Sound Level Meter	I.491835	3 Jan 2022
Rion NC-74 Sound Level Calibrator	34504770	11 Feb 2022

Table 3.2 Monitoring Equipment Used in Monitoring

3.3. Monitoring Methodology and QA/QC results

Air Quality

3.3.1. The 1-hour TSP monitor, portable dust meters (Sibata Digital Dust Indicator Model LD-5R) was used for the impact monitoring. The 1-hour TSP meters provides a real time 1-hour TSP measurement based on 90° light scattering. Three 1-hour TSP level were logged per every six days.

- 3.3.2. The 24-hour TSP monitor, High Volume Samplers (Tisch TE-5170X High Volume Air Sampler) were used for the impact monitoring. The 24-hour TSP monitoring consists of the following:
 - ◆ The HVS was set at the monitoring location, with electricity supply connected and secured:
 - ♦ HVS was calibrated before commencing the 1st measurement;
 - ◆ The filter paper was weight and provided by HOKLAS lab (Acumen Laboratory and Testing Limited and ALS Technichem (HK) Pty Ltd) before and after the sampling. Certificate of HOKLAS accredited laboratory can be referred to Appendix J;
 - The airflow over time during sampling process was recorded by the HVS.
- 3.3.3. HVSs were free-standing with no obstruction. The following criteria were considered in the installation of the HVS:
 - ◆ Appropriate support to secure the samples against gusty wind needed to be provided the monitoring station;
 - ◆ A minimum of 2m separation from walls, parapets and penthouses was required for rooftop samplers;
 - ◆ No furnace or incinerator flues was nearby;
 - ◆ Airflow around the sampler was unrestricted; and
 - Permission could be obtained to set up the samplers and gain access to the monitoring station.

3.3.4. Preparation of Filter Papers

- Glass fiber filters were labelled and sufficient filters that were clean and without pinholes were selected;
- ◆ All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25°C and not varied by more than ±3°C; the relative humidity (RH)was 40%; and
- ◆ Acumen Laboratory and Testing Limited and ALS Technichem (HK) Pty Limited, as HOKLAS accredited laboratory, implemented comprehensive quality assurance and quality control programmes on the filters.

3.3.5. Field Monitoring

- ◆ The power supply was checked to ensure that the HVS was working properly;
- ◆ The filter holder and area surrounding the filter were cleaned;
- ◆ The filter holder was removed by loosening the foul bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully;
- ◆ The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter;
- ◆ The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges;
- The shelter lid was closed and secured with an aluminum strip;
- ♦ The HVS was warmed- up for about 5 minutes to establish run- temperature conditions:

- A new flow rate record sheet was inserted into the flow recorder;
- ◆ The flow rates of the HVS was checked and adjusted to between 0.64-1.52m³min⁻¹, which was within the range specified in the EM&A Manual (i.e. 0.6-1.7m³min⁻¹);
- ◆ The programmable timer was set for a sampling period of 24 hours, and the starting time, weather condition and filter number were recorded;
- ◆ The initial elapsed time was recorded;
- ◆ At the end of sampling, the sampled filter was removed carefully and folded in half so that only surfaces with collected particulate matter were in contact;
- ◆ The filter paper was placed in a clean plastic envelope and sealed; all monitoring information was recorded on a standard data sheet and
- ◆ The filters were sent to (Acumen Laboratory and Testing Ltd and ALS Technichem (HK) Pty Ltd) for analysis.

3.3.6. Maintenance and Calibration

- ◆ The HVS and their accessories were maintained in a good working condition. For example, motor brushes were replaced routinely and electrical wiring was checked to ensure a continuous power supply; and
- ♦ The flow rate of each HVS with mass flow controller was calibrated using an orifice calibrator, Initial calibrations of the dust monitoring equipment were conducted upon installation and prior to commissioning. Five- point calibration was carried out for HVS using TE-5025 Calibration Kit. HVS is calibrated bimonthly. The calibration records for the HVS is given in Appendix H.

3.3.7. Wind Data Monitoring

◆ The wind speed has been recorded from Hong Kong Observatory- King's Park meteorological station, along with portable wind speed meter stand by as back up when the information are not available from HKO.

Noise

- 3.3.8. All noise measurements by the meter were set to FAST response and on the A-weighted equivalent continuous sound pressure level (L_{eq}) in decibels dB(A). $L_{Aeq(30min)}$ was used as the monitoring metric for the time period between 0700 -1900 hours on normal weekdays. The measured noise levels were logged every 5 minutes throughout the monitoring period.
- 3.3.9. Prior to the noise measurement, the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Checking was conducted before and after the monitoring. The calibration level before and after the noise measurement is agreed to within 1.0 dB(A).
- 3.3.10. Noise measurements should not be made in presence of fog, rain, wind with a steady speed exceeding 5 ms⁻¹ or wind with gusts exceeding 10 ms⁻¹. The wind speed was checked with a portable wind speed meter capable of measuring with speeds in ms⁻¹.

3.4. Monitoring Locations

Air Quality

3.4.1. During the site visit, both of the original proposed dust monitoring locations were rejected due to the condition at The Coronation was not favourable for monitoring and the access was declined by the management office of Hong Kong Community College (HKCC) of PolyU. Two alternative air monitoring stations Yau Ma Tei Catholic Primary School (Hoi Wang Road) and Man Cheong Building had been proposed by ET and approved by IEC. 2 designated air monitoring locations were identified and agreed with IEC and EPD. Details of air monitoring stations are described in Table 3.3. The location plan of air quality monitoring stations is shown in Appendix K.

Table 3.3 Location of the Dust Monitoring Stations

Air Quality Monitoring Station	Dust Monitoring Station
W-A1	Yau Ma Tei Catholic Primary School (Hoi Wang Road)
W-A6	Man Cheong Building

Noise

3.4.2. During the site visit, one of the original proposed noise monitoring locations Tak Cheong Building was rejected by the president of the owner's corporation. Alternative noise monitoring station Hydan place had been proposed by ET and approved by IEC. 4 noise sensitive receivers designated noise monitoring locations were identified and agreed with IEC and EPD. The designated monitoring stations are identified and access was granted by the premises. The details of noise monitoring stations are described in Table 3.4 and the location plan of noise monitoring station is shown in Appendix K.

Table 3.4 Noise Monitoring Stations

Noise Monitoring Station	Identified Noise Monitoring Station	Type of Measurement
W-N1A	Yau Ma Tei Catholic Primary School (Hoi Wang Road)	Façade
W-N18	Hydan Place	Façade
W-N25A	Prosperous Garden Block 1	Façade
W-P11	The Coronation Tower 1	Façade

- 3.5. Monitoring date, time, frequency and duration
- 3.5.1. A summary of impact monitoring duration, sampling parameter and frequency is presented in Table 3.5.

Impact Duration **Sampling Parameter Frequency Monitoring** 1-hour continuous 1-hour TSP Dust 3 times per six days measurement 24-hour continuous Dust 24-hour TSP Once per six days sampling 30-minute continuous $L_{eq 30 min}$, Noise Once per week (0700 - 1900)measurement L₁₀ and L₉₀ as reference.

Table 3.5 Summary of Impact Monitoring Programme

3.6. Result Summary

Air Quality

3.6.1. According to our field observations, the major dust source identified at the designated air quality monitoring stations in the reporting month are summarised in Table 3.6.

Table 3.6 Observation at Dust Monitoring Stations

Monitoring Station	Major Dust Source	
W-A1	Nearby traffic	
W-A6	Nearby traffic	

- 3.6.2. Air quality impact monitoring for the reporting month was carried out on 1, 7, 12, 18, 24 and 30 November 2022.
- 3.6.3. The results for 1-hour TSP and 24-hour TSP are summarized in Table 3.7 and Table 3.8. The measurement data and details of influencing factors such as weather conditions and site observation are presented in Appendix L.

Table 3.7 Summary of 1-hour TSP Monitoring Results

Monitoring Location	Range(µg/m³)	Action Level(μg/m3)	Limit Level(µg/m3)
W-A1	46 - 66	319	500
W-A6	53 - 74	306	500

Table 3.8 Summary of 24-hour TSP Monitoring Results

Monitoring Location	Range(µg/m³)	Action Level(μg/m3)	Limit Level(µg/m3)	
W-A1	12 - 27	167	260	
W-A6	11 - 82	166	260	

Noise

3.6.4. According to our field observations, the major noise source identified at the designated noise monitoring station in the reporting month are summarised in Table 3.9:

Monitoring Station	Major Noise Source
W-N1A	Nearby traffic
W-N18	Nearby traffic
W-N25A	Nearby traffic
W-P11	Nearby traffic

Table 3.9 Observation at Noise Monitoring Stations

- 3.6.1. The construction noise impact monitoring for the reporting month was carried out on 1, 7, 12, 18, 24 and 30 November 2022.
- 3.6.2. The result for noise monitoring is summarized in Table 3.10. The measurement data are shown in Appendix M.

Time **Monitoring** Range, dB(A) **Parameter** Period location **Action Level** Limit Level# \mathbf{L}_{eq} L_{10} L_{90} 70dB(A) or 65 56.9 - 58.0W-N1A* 60.0 - 62.562.3 - 63.8dB(A) during examination 70.2 - 72.073.1 - 74.366.3 - 68.1W-N18 Normal When one working Leq documented 30min hour from complaint is 0700-1900 received W-N25A 68.3 - 71.171.6 - 74.165.8 - 68.275dB(A)# W-P11 65.1 - 67.167.0 - 69.063.2 - 65.1

Table 3.10 Summary of Noise Monitoring Results

Remarks:

- 1. # If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit by the Noise Control Authority have to be followed.
- 2. *Examination was carried out at Yau Ma Tei Catholic Primary School between 14 to 22 November 2022. The limit level of W-N1A would be 65 dB(A) on 18 November 2022. The limit level of W-N1A would be 70 dB(A) on 1, 7, 12, 24 and 30 November 2022.

Waste management

3.6.3. The waste generated from this Project includes inert C&D materials, and non-inert C&D materials. Non-inert C&D materials are made up of general refuse, vegetative wastes and recyclable wastes such as plastics and paper/cardboard packaging waste. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types

of waste generated in the reporting month are summarised in Table 3.11. Details of cumulative waste management data are presented as a waste flow table in Appendix N.

Table 3.11 Quantities of waste generated from the Project

	Quantity					
Reporting period Mate			Non-inert C&D Materials			
		Others, e.g.	Recy	ycled material	s	
	Inert C&D Materials (in 'tonnes)	Chemical Waste (in'000 Kg)	General Refuse disposed	Paper/card board (in '000 Kg)		Metals (in '000 Kg)
November-2022	12482.80	0.00	49.80	0.10	0.00	0.00

4. SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS

4.1. The Environmental Complaint Handling Procedure is shown in below Table 4.1:

Table 4.1 Environmental Complaint Handling Procedure

Complaint Received via Project Hotline		Complaint Received via 1823 or from other government departments				
Contractor notify ER, ET	and IEC	ER notify Contractor, ET and IEC				
		•				
Contractor log complain	<u> </u>	o the complaint database. Contractor, ER and ET to gation of complaint				
If complaint is considered	d not valid	If complaint is found valid				
ET or ER to reply the complainant if necessary		Contractor to identify and implement remedial measures in consultation with the IEC, ET and ER.				
		The ER, ET and IEC to review the effectiveness of the Contractor's remedial measures and the updated situation; ET to undertake additional monitoring and audit to verify the situation if necessary, and oversee that circumstances leading to the complaint do not recur. ER to conduct further inspection as necessary.				
70.1						
If the complaint is referred by the EPD, the Contractor to prepare interim report on the status of the complaint investigation and follow-up actions stipulated above, including the details of the remedial measures and additional monitoring identified or already taken, for submission to EPD within the time frame assigned by the EPD						
	1 04 1 1	ulta of the investigation subsequent estimately and				

The ET to record the details of the complaint, results of the investigation, subsequent actions taken to address the complaint and updated situation including the effectiveness of the remedial measures, supported by regular and additional monitoring results in the monthly EM&A reports

- 4.2. Should non-compliance of the criteria occur, action in accordance with the Event and Action Plan in Appendix D and Appendix E shall be carried out.
- 4.3. Four Action Levels of construction noise were triggered during the reporting month as documented complaints related to construction noise from works areas at Zone 3 Noise Enclosure and Zone D3, whereas two complaints were received on 11 November 2022, two complaints were received on 14 November 2022 and 17 November 2022 respectively. No exceedance of Limit Level of construction noise was recorded in the reporting month. No exceedance of the Action and Limit Level of 24-hour TSP and 1-hour TSP was recorded in the reporting month.
- 4.4. Four noise related complaints were received in the reporting month, whereas two complaints were received on 11 November 2022, two complaints were received on 14 November 2022 and 17 November 2022 respectively. Two complaints were concluded as non-project related. After investigation with Contractor, precautionary measures had been proposed to the Contractor by ET. The interim report for the complaint is shown in Appendix Q.
- 4.5. No non-compliance was reported in the reporting month.
- 4.6. No notification of summon and prosecution was received in the reporting period.
- 4.7. Statistics on complaints, notifications of summons and successful prosecutions are summarized in Appendix O.

5. EM&A SITE INSPECTION

- 5.1. Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, four (4) site inspections were carried out on 3, 10, 17 and 24 November 2022, along with bi-weekly inspection of the implementation of landscape and visual mitigation measures conducted on 10 and 24 November 2022.
- 5.2. One joint site inspection with IEC also undertaken on 10 November 2022. Minor deficiencies were observed during weekly site inspection. Key observations during the site inspections are summarized in Table 5.1.

Environmental Observations Date Follow-up Status 1. Cement bags at Zone 3 Noise 1. Cement bags had been covered with Enclosure should be covered with impervious sheeting. impervious sheeting at 3 sides. 2. Noise barrier had been applied for the 3 November 2022 2. Noise barrier should be applied for the breaker. breaker at Zone B1. General refuse at Zone B2 should be stored in enclosed bin. Tree protection zone at Zone B3 Tree protection zone had been kept should be clear of construction clean. materials. 2. Chemical oil had been treated. 10 November 2022 2. Chemical oil was observed at Zone D, which should be treated as followed by Code of Practice of Chemical Waste. 1. Cement bags at Zone F should be 1. Cement bags had been removed. covered with impervious sheeting at 3 2. Construction materials had been sides. cleared at the tree protection zone. 17 November 2022 Tree protection zone at Zone D should 3. Construction materials had been be clear of construction materials. removed. 3. Construction materials at Zone D should be stored properly. Chemicals at Zone A should be stored 1. Chemicals had been removed. properly with label. Chemical wastes had been treated and 24 November 2022 Chemical wastes at Zone 3 should be stored in chemical waste storage area. treated as followed by Code of Practice of Chemical Waste.

Table 5.1 Site Observations

- 5.3. The Contractor had rectified all observation identified during environmental site inspection in the reporting period.
- 5.4. According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents are implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in Appendix F.

6. FUTURE KEY ISSUES


6.1. The construction activities provided by Main Contractor in the next reporting month are:


Construction Activities to be undertaken

- Removal of Struts and construction of Lower Ventilation Duct Columns at Zone A
- Installation of Underground Utilities Hanger Support, exposure of box culvert and plugging of abandoned pipe at Zone B
- Install hanger support for existing Underground Utilities under traffic deck, excavation to roof slab in Zone B, C and D
- Construction of ceiling slab at Zone B1
- Underground Utilities diversion and D-wall construction at Zone B3
- Underground Utilities diversion, jet grouting, pre-boring works and D-wall construction at Zone F
- DN1800 drainage diversion work and ground improvement at Dickson/Tak Cheong Buildings (TAM Grouting, jet grouting) works at Zone G
- Works for reprovisioning of Gascogine Road Flyover at HKAA area: Falsework erection and end span construction for P7L
- Bridge Works:
 - i. FT1- bridge deck construction for P3L
 - ii. FT2- bridge deck construction for P2L
- Temporary parapet and noise barriers construction for P4L to P6L
- Complete remaining socketted H-pile works for middle and west side of F02 Noise Enclosure in Zone 3, continue excavation and lateral support and construction works for pile caps and ground beams construction for middle / east foundation for F02 Noise Enclosure
- Erection of Y columns, side columns and main beams for Noise Enclosure F02 in Zone 3 (night works)
- Works at Zone 2 Noise Enclosure scheduled as the following:
 - i. Column E & A Excavation and Lateral Support works and pile cap construction
 - ii. Column G Permanent diversion of uncharted drainage pipe
 - iii. Columns A1 Construct temporary reinforced concrete pile cap and erect steel tower
 - iv. Column C Complete design and fabrication of steel footing and install steel footing
 - v. Columns D Temporary socketted H-pile works
- Noise Enclosure steelworks fabrication at Fabrication Yard in Zhuhai, China
- Monitoring of instrumentation for all areas
- 6.2. Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise and waste management.
- 6.3. The tentative schedule of regular construction noise, 1-hour TSP and 24-hour TSP monitoring in the next reporting period is presented in Appendix P.
- 6.4. The construction programme for the Project for the next reporting month is presented in Appendix B.

7. CONCLUSION AND RECOMMENDATIONS

- 7.1. This 56th monthly EM&A Report presents the EM&A works undertaken during the period from 1 November 2022 to 30 November 2022 in accordance with the EM&A Manual and the requirement under EP- 457/2013/D and FEP-03/457/2013/D.
- 7.2. Four Action Levels of construction noise were triggered during the reporting month as documented complaints related to construction noise from works areas at Zone 3 Noise Enclosure and Zone D3, whereas two complaints were received on 11 November 2022, two complaints were received on 14 November 2022 and 17 November 2022 respectively. No exceedance of Limit Level of construction noise was recorded in the reporting month. No exceedance of the Action and Limit Level of 24-hour TSP and 1-hour TSP was recorded in the reporting month.
- 7.3. Weekly environmental site inspections were conducted during the reporting period. Joint site inspection with IEC were carried out on 10 November 2022. Minor deficiency was observed during site inspection and was rectified within the specified deadlines. The environmental performance of the Project was therefore considered satisfactory.
- 7.4. Four noise related complaints were received in the reporting month, whereas two complaints were received on 11 November 2022, two complaints were received on 14 November 2022 and 17 November 2022 respectively. Two complaints were concluded as non-project related. After investigation with Contractor, precautionary measures had been proposed to the Contractor by ET. The interim report for the complaint is shown in Appendix Q.
- 7.5. No non-compliance was reported in the reporting month.
- 7.6. No notification of summons or prosecution was received in the reporting month.
- 7.7. The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.



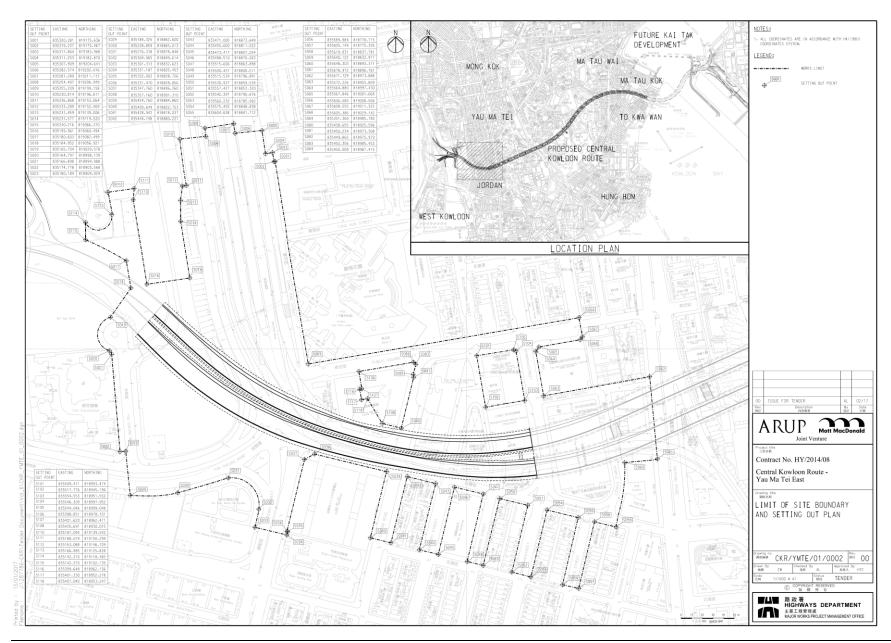





Appendix B Construction Programme

Construction Programme					
activity Name	Durati	on Start	Finish		
HY/2014/08 Central Kowloom Route - Yau Ma Tei East	2996	8-Jan-18	22-Mar-26		
Construction Works	2987	17-Jan-18	22-Mar-26		
emporary Traffic Management in Underground (Portion 11 & 12)	1722	29-Sep-19	15-Jun-24		
Forks on Northern & Southern Parts of YMT Muhi-Storey Car Park Building	674	1-Sep-21	6-Jul-23		
off Works within TMTSC, Maintenance Depot Area, Public Square St/Kansu St Rest Garden, Access Road	2492	17-Jan-18	12-Nov-24		
reservation and Protection of Existing Trees	2622	17-Jan-18	22-Mar-25		
stablishment Works	365	23-Mar-25	22-Mar-26		
II Works in Underground	1195	14-Feb-22	23-May-25		
completion of Noise Enclosure	1602	26-Aug-20	13-Jan-25		
Il Remaining Works not Covered in Other Section	2482	6-Jun-18	22-Mar-25		
Construction of C&C Tunnel Eastbound	2418	17-Jan-18	30-Aug-24		
Construction of C&C Tunnel Westbound	2549	17-Jan-18	8-Jan-25		
&C Tunnel Works within Portion 13 & 20A, Cul-de-sac at Portion 20B & 24	1749	7-Apr-18	19-Jan-23		
temolition of Southern Part of Ex. YMT Multi-Storey Car Park Building	146	6-Feb-23	1-Jul-23		
RF Reprovisioning	1759	16-Dec-19	8-Oct-24		
Completion of Diaphragm Walls and Boof Stabs of C&C Tunnels within Portion 27 and 28	1	7-Feb-23	7-Feb-23		

Contract No. HY/2014/08 Environmental Monitoring & Auditing
Appendix C
Project Organization Chart

Project O-Chart

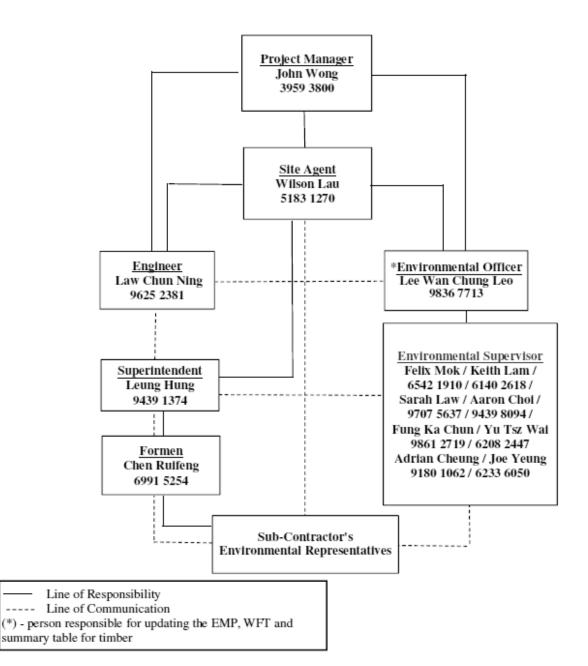



EVENT	ACTION							
EVENI	ET	IEC	ER	CONTRACTOR				
ACTION LEV	ACTION LEVEL							
1.Exceedance for one sample	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; Increase monitoring frequency to daily. 	 Check monitoring data submitted by ET; Check Contractor's working method. 	1. Notify Contractor.	 Rectify any unacceptable practice; Amend working methods if appropriate. 				
2.Exceedance for two or more consecutive samples	 Identify source; Inform IEC and ER; Advise the ER on the effectiveness of the proposed remedial measures; Repeat measurements to confirm findings; Increase monitoring frequency to daily; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with IEC and ER; If exceedance stops, cease additional monitoring. 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Supervise Implementation of remedial measures. 	Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented.	 Submit proposals for remedial to ER within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate. 				
LIMIT LEVEL			,	,				
1.Exceedance for one sample	Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and	 Check monitoring data submitted by ET; Check Contractor's working method; 	Confirm receipt of notification of failure in writing; Notify Contractor;	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC				


EVENT	ACTION			
EVENI	ET	IEC	ER	CONTRACTOR
	 EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	3. Ensure remedial measures properly implemented.	within 3 working days of notification; Implement the agreed proposals; 4. Amend proposal if appropriate.
2.Exceedance for two or more consecutive samples	 Notify IEC, ER, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. 	 Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Note:

ET – Environmental Team

ER – Engineer's Representative

IEC – Independent Environmental Checker



EVENT		ACTIO	ON	
	ET	IEC	ER	CONTRACTOR
Action Level	 Identify source, investigate the causes of exceedance and propose remedial measures; Notify IEC and Contractor; Report the results of investigation to the IEC, ER and Contractor; Discuss with the Contractor and formulate remedial measures; Increase monitoring frequency to check mitigation effectiveness. 	 Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented 	Submit noise mitigation proposals to IEC; Implement noise mitigation proposals.
Limit	 Identify source; Inform IEC, ER, EPD and Contractor; Repeat measurements to confirm findings; Increase monitoring frequency; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Inform IEC, ER and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions 	 Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated.

EVENT	ACTION							
	ET	IEC	ER	CONTRACTOR				
	and keep IEC, EPD and ER informed of the results;		abated.					
	8. If exceedance stops, cease additional monitoring.							

Note:

ET – Environmental Team

IEC – Independent Environmental Checker

ER – Engineer's Representative



Appendix F
Environmental Mitigation Implementation
Schedule (EMIS)

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
			Constru	ction Dust Impact				
S4.3.10	D1	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	APCO To control the dust impact To meet HKAQO and TM-EIA criteria	Implemented, deficiency rectified after observation
\$4.3.10	D2	 Mitigation measures in form of regular watering under a good site practice should be adopted. Watering once per hour on exposed worksites and haul road should be conducted to achieve dust removal efficiencies of 91.7%. While the above watering frequencies are to be followed, the extent of watering may vary depending on actual site conditions but should be sufficient to maintain an equivalent intensity of no less than 1.3 L/m² to achieve the dust removal efficiency. 	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	APCO To control the dust impact To meet HKAQO and TM-EIA criteria	• Implemented
S4.3.10	D3	 Proper watering at exposed spoil should be undertaken throughout the construction phase; Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; A stockpile of dusty material should not be 	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	Construction stage	APCO To control the dust impact To meet HKAQO and TM-EIA criteria	Implemented, deficiency rectified after observation

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		extended beyond the pedestrian barriers, fencing or traffic cones; The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle. Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores; When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided and properly maintained as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period; The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials; Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 continuously; Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; Any skip hoist for material transport should be totally enclosed by impervious sheeting; Every stock of more than 20 bags of cement or dry-pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides; Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabilizer within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies. 						
\$4.3.10	D6	Implement regular dust monitoring under EM&A programme during the construction stage.	Monitoring of dust impact	Contractor	Selected rep. dust monitoring station	Construction stage	• TM-EIA	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S5.4.1	N1	 Implement the following good site practices: Only well-maintained plant should be operated onsite and plant should be serviced regularly during the construction programme; Machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; Plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs; Silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works; Mobile plant should be sited as far away from NSRs as possible and practicable; Material stockpiles, mobile container site office and other structures should be effectively utilized, where practicable, to screen noise from on-site construction activities. 	Control construction airborne noise	Contractor	All construction sites	Construction stage	• Annex 5, TM- EIAO	• Implemented
S5.4.1	N2	Install temporary hoarding located on the site boundaries between noisy construction activities and NSRs. The conditions of hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening	Contractor	All construction sites	Construction stage	• Annex 5, TM- EIAO	Implemented
S5.4.1	N3	Install movable noise barriers (typical design is wooden framed barrier with a small-cantilevered on a skid footing with 25mm thick internal sound absorptive lining), acoustic mat or full enclosure,	Sreen the noisy plant items to be used at all construction	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM- EIAO	Implemented, deficiency rectified after observation

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		screen the noisy plants including air compressors, generators and handheld breakers, etc.	sites					
S5.4.1	N4	Use 'Quiet plant'	Reduce the noise levels of plant items	Contractor	All construction sites where practicable	Construction stage	Annex 5, TM- EIAO	Implemented
S5.4.1	N5	Loading/ unloading activities should be carried out inside the full enclosure of mucking out points.	Reduce the noise levels of loading/ unloading activities	Contractor	Mucking out locations	Construction stage	• Annex 5, TM- EIAO	Implemented
S5.4.1	N6	Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction airborne noise	Contractor	All construction sites where practicable	Construction stage	• Annex 5, TM- EIAO	Implemented
S5.4.1	N7	Implement a noise monitoring programme under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected rep. noise monitoring station	Construction stage	• TM-EIAO	Implemented

Water Quality (Construction Phase)

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
\$6.9.1.1	W1	In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN1/94), construction phase mitigation measures shall include the following: Construction Runoff • At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction; • The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt/ sediment trap. The sediment/ silt traps should be incorporated in the permanent drainage channels to enhance deposition rates; • The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/ sand traps should be 5 minutes under	To minimize water quality impact from the construction site runoff and general construction activities	Contractor	All construction sites where practicable	Construction stage	Water Pollution Control Ordinance ProPECC PN 1/94 TM-EIAO TM-DSS	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		maximum flow conditions. Sizes may vary depending upon the flow rate, but for a flow rate of 0.1 m3/s a sedimentation basin of 30 m3 would be required and for a flow rate of 0.5 m3/s the basin would be 150 m3. The detailed design of the sand/silt traps shall be undertaken by the contractor prior to the commencement of construction; • All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. Exposed slope surfaces should be covered by tarpaulin or other means; • The overall slope of the site should be kept to a minimum to reduce the erosive potential of surface water flows, and all traffic areas and access roads protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during prolonged periods of inclement weather and the reduction of surface sheet flows; • All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas; • Measures should be taken to minimize the ingress of site drainage into excavations. If the excavation						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities; Open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m3 should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system; Manholes should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers; Precautions be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes; All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and site wheel washing facilities should be provided at every construction						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel wash bay to the public road should be paved with sufficient backfall toward the wheel wash bay to prevent vehicle tracking of soil and silty water to public roads and drains; Oil interceptors should be provided in the drainage system downstream of any oil/ fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain; Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts; All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby; Adopt best management practices; All earth works should be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to November) as far as practicable.						

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
\$6.9.1.2	W2	 Tunneling Works and Underground Works Cut-&-cover tunneling work should be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to November) as far as practicable. Uncontaminated discharge should pass through sedimentation tanks prior to off-site discharge; The wastewater with a high concentration of SS should be treated (e.g. by sedimentation tanks with sufficient retention time) before discharge. Oil interceptors would also be required to remove the oil, lubricants and grease from the wastewater; Direct discharge of the bentonite slurry (as a result of D-wall) is not allowed. It should be reconditioned and reused wherever practicable. Temporary storage locations (typically a properly closed warehouse) should be provided on site for any unused bentonite that needs to be transported away after all the related construction activities area completed. The requirements in ProPECC PN 1/94 should be adhered to in the handling and disposal of bentonite slurries. 	To minimize construction water quality impact from tunneling works	Contractor	All tunneling portion	Construction stage	Water Pollution Control Ordinance ProPECC PN 1/94 TM-DSS TM-EIAO	• Implemented
S6.9.1.3	W3	Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide	To minimize water quality from sewage effluent	Contractor	All construction sites where practicable	Construction stage	Water Pollution Control Ordinance TM-DSS	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.						
S6.9.1.5	W4	 No direct discharge of groundwater from contaminated areas should be adopted. A discharge license under the WPCO through the Regional Office of EPD for groundwater discharge should be applied. Prior to the excavation works within these potentially contaminated areas, the groundwater quality should be reviewed during the process of discharge license application. The compliance to the Technical Memorandum on Standards for Effluents Discharged into Drainage on Sewerage Systems, Inland and Coastal Waters (TM-DSS) and the existence of prohibited substance should be confirmed. If the review results indicated that the groundwater to be generated from the excavation works would be contaminated, the contaminated groundwater should be either properly treated in compliance with the requirements of the TM-DSS or properly recharged into the ground. If wastewater treatment is deployed, the wastewater treatment unit shall deploy suitable treatment process (e.g. oil interceptor / activated carbon) to reduce the pollution level to an 	To minimize groundwater quality impact from contaminated area	Contractor	Excavation areas where contamination is found	Construction stage	Water Pollution Control Ordinance TM-DSS TM-EIAO	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		acceptable standard and remove any prohibited substances (e.g. TPH) to undetectable range. All treated effluent from wastewater treatment plant shall meet the requirements as stated in TM-DSS and should be discharged into the foul sewers. • If groundwater recharging wells are deployed, recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in the Section 2.3 of TM-DSS. The baseline groundwater quality shall be determined prior to the selection of the recharge wells, and submit a working plan (including the laboratory analytical results showing the quality of groundwater at the proposed recharge location(s) as well as the pollutant levels of groundwater to be recharged) to EPD for agreement. Pollution levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the recharge well. Prior to recharge, any prohibited substances such as TPH products should be removed as necessary by installing the petrol interceptor.						
\$6.9.1.6		Accidental Spillage In order to prevent accidental spillage of chemicals, the following is recommended:	To minimize water quality impact from accidental	Contractor	All construction site where practicable	Construction stage	Water Pollution Control Ordinance	Implemented

			Objectives -f					
EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		All the tanks, containers, storage area should be bunded and the locations should be locked as far as possible from the sensitive watercourse and stormwater drains; The Contractor should register as a chemical waste producer if chemical wastes would be generated. Storage of chemical waste arising from the construction activities should be stored with suitable labels and warnings. Disposal of chemical wastes should be conducted in compliance with the requirements as stated in the Waste Disposal (Chemical Waste) (General) Regulation.	spillage				Propecc PN 1/94 TM-EIAO TM-DSS	
			Waste Manage	ement (Construction	Waste)			
\$7.4.1	WM1	Geological assessment should be carried out by competent persons on site during excavation to identify materials which are not suitable to use as aggregate in structural concrete (e.g. volcanic rock, Aplite dyke rock, etc.). Volcanic rock and Aplite dyke rock should be separated at the source sites as far as practicable and stored at designated stockpile area preventing them from delivering to crushing facilities. The crushing plant operator should also be reminded to set up measures to prevent unsuitable rock from ending up at concrete	Separation of unsuitable rock from ending up at concrete batching plants and be turned into concrete for structural use	Contractor	All construction sites	Construction stage	• DEVB (W) No. 6/2010	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
\$7.5.1	WM2	batching plants and be turned into concrete for structural use. Details regarding control measures at source site and crushing facilities should be submitted by the Contractor for the Engineer to review and agree. In addition, site records should also be kept for the types of rock materials excavated and the traceability of delivery will be ensured with the implementation of Trip Ticket System and enforced by site supervisory staff as stipulated under DEVB TC(W) No. 6/2010 for tracking of the correct delivery to the rock crushing facilities for processing into aggregates. Alternative disposal option for the reuse of volcanic rock and Aplite Dyke rock, etc. should be explored. Construction and Demolition Material Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement; Carry out on-site sorting; Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; Adopt 'selective demolition' technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible; Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified; and	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction stage	Land (Miscellaneo us Provisions) Ordinance Waste Disposal Ordinance ETWB TCW No. 19/2005	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		• Implement an enhanced Waste Management Plan similar to ETWBTC (Works) No. 19/2005 – "Environmental Management on Construction Sites" to encourage on-site sorting of C&D materials and to minimize their generation during the course of construction.						
\$7.5.1	WM3	 Standard formwork or pre-fabrication should be used as far as practicable in order to minimize the arising of C&D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage; The Contractor should recycle as much of the C&D materials as possible on-site. Public fill and C&D waste should be segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and storage. 	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction stage	Land (Miscellaneo us Provisions) Ordinance Waste Disposal Ordinance ETWB TCW No. 19/2005	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
\$7.5.1	WM5	 All construction plant and equipment shall be designed and maintained to minimize the risk of silt, sediments, contaminants or other pollutants being released into the water column or deposited in the locations other than designated location; All vessels shall be sized such that adequate draft is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; Before moving the vessels which are used for transporting dredged material, excess material shall be cleaned from the decks and exposed fittings of vessels and the excess materials shall never be dumped into the sea except at the approved locations; Adequate freeboard shall be maintained on barges to ensure that decks are not washed by wave action. The Contractors shall monitor all vessels transporting material to ensure that no dumping outside the approved location takes place. The Contractor shall keep and produce logs and other records to demonstrate compliance and that journeys are consistent with designated locations and copies of such records shall be submitted to the engineers; The Contractors shall comply with the conditions in the dumping licence. 	To control pollution due to marine sediment	Contractor	Along CKR alignment	Construction stage	• ETWB TCW No. 34/2002	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 All bottom dumping vessels (Hopper barges) shall be fitted with tight fittings seals to their bottom openings to prevent leakage of material; The material shall be placed into the disposal pit by bottom dumping; Contaminated marine mud shall be transported by spit barge of not less than 750m3 capacity and capable of rapid opening and discharge at the disposal site; Discharge shall be undertaken rapidly and the hoppers shall be closed immediately. Material adhering to the sides of the hopper shall not be washed out of the hopper and the hopper shall remain closed until the barge returns to the disposal site. For Type 3 special disposal treatment, sealing of contaminant with geosynthetic containment before dropping designated mud pit would be a possible arrangement. A geosynthetic containment method is a method whereby the sediments are sealed in geosynthetic containers and, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping at the disposal site, thereby fulfilling the requirements for fully confined mud disposal. 						
S7.5.1	WM6	 Chemical Waste Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be handled in 	Control the chemical waste and ensure proper storage,	Contractor	All construction sites	Construction stage	• Waste Disposal (Chemical Waste)	Implemented, deficiency rectified after observation

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes; Containers used for the storage of chemical wastes should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed, have a capacity of less than 450 L unless the specification has been approved by EPD, and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the regulation; The storage area for chemical wastes should be clearly labelled and used solely for the storage of chemical waste, enclosed on at least 3 sides, have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20% of the total volume of waste stored in that area, whichever is the greatest, have adequate ventilation, covered to prevent rainfall entering, and arranged so that incompatible materials are adequately separated; Disposal of chemical waste should be via a licensed waste collector, be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Centre which also offers a chemical waste collection service and can supply the necessary storage containers, or be to a reuser of the waste, under approval from EPD.	handling and disposal				(General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Waste	

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
\$7.5.1	WM7	 General Refuse General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes; A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law. Aluminum cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible; Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be considered by the Contractor. 	Minimize production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	Construction stage	Waste Disposal Ordinance	Implemented, deficiency rectified after observation
		Scheme should be considered by the contractor.	Land Contamin	ation				
S8.9 & Appendix 8.4	LC2	Prior to commencement of the excavation works at the contamination zone, the zone should be clearly marked out on site and the surface levels recorded. Excavation of contaminated material should be undertaken using dedicated earth-moving plant. The excavated contaminated soils would be stockpiled at designated area on site and covered by sheet to prevent dispersion of contamination	The contaminated soil will be excavated for on-site reuse	Contractor	РВН4	Prior to commencement of construction works within the contaminated area	• Practice Guide (PG) for Investigation and Remediation of Contaminate d Land	Implemented

EIA Ref.	EM&A Log Ref.	Reco	mmended Mitiga	tion Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		during stockpiling. The Contractor should pay attention to the selection of suitable groundwater lowering schemes and discharge points if the groundwater table is higher than the contaminated soils during excavation. The Contractor should also obtain a valid Water Pollution Control Ordinance (WPCO) discharge licence from EPD where applicable.							Guidance Notes for Contaminate d Land Assessment and Remediation Guidance	
S8.9 & Appendix 8.4	LC3	Following completion of the excavation to the specified depth, at least one sample from the base of the excavation and four samples evenly distributed along the boundary of the excavation shall be taken for a closure assessment testing. The acceptance criterion is shown below:						Manual for Use of Risk- Based Remediation Goals (RBRGs) for Contaminate	Implemented	
		Locations Testing Acceptance requirement Criteria PBH4 PCBs RBRGs (Public Park) • If the results of analysis below the RBRGs (Public Park), no further excavation will be required. If the analysis indicates presence of contamination (i.e. noncompliance of the acceptance criteria), further excavation shall be carried out in 0.5m increment vertically and/or horizontally depending on the location(s) of the sample(s) which has exceeded the acceptance criteria. Further sampling shall also be conducted for compliance testing. The process of						d Land Management		

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
Appendix 8.4	LC4	excavation, sampling and compliance testing should continue until all contaminated materials are removed and should be supervised by a Land Contamination Specialist. A Remediation Report (RR) to demonstrate adequate clean-up shall be prepared and submitted to EPD for endorsement prior to the commencement of any construction/development works within the sites. No construction/development works shall be carried out						• Implemented
		prior to the endorsement of the RR by EPD.		l Hazard to Life				
S9.18	H1	Blasting activities regarding transport and use of explosives should be supervised and audited by competent site staff to ensure full compliance with the blasting permit conditions.	To ensure that the risks from the proposed explosives handling and transport would be acceptable	Contractor	Works areas at which explosives would be used	Construction stage	Dangerous Goods Ordinance	• N/A
S9.6, para.4	H2	Detonators shall not be transported in the same vehicle with other Category 1 Dangerous Goods.	To reduce the risk of explosion during the transport of cartridged emulsion	Contractor	-	Construction stage	Dangerous Goods Ordinance	• N/A
S9.6, para.8	Н3	The explosives delivery trucks should be approved by Mines Division and should meet the regulatory requirements for transport of explosives.	To comply with the requirements for approval of an explosives	Contractor	-	Construction stage	Dangerous Goods Ordinance	• N/A

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
			delivery vehicle					
S9.10, para.7 and S9.18	H4	Blast cover should be provided for shaft at HMT, and kept closed during blasting. Provision of blast doors or heavy duty blast curtains should be implemented at the shaft to prevent flyrock and control the air overpressure.	To ensure safe use of explosives	Contractor	Shaft	Construction stage	-	• N/A
S9.16	H5	Only the required quantity of explosives for a particular blast should be transported to avoid the return.	To reduce risks during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
\$9.18	H7	The approved truck dedicated for transport of explosives should comply with the "Guidance Note on Requirements for Approval of an Explosives Delivery Vehicle" issued by CEDD Mines Division. The truck should be periodically inspected and properly maintained in good operation conditions. The fuel carried in the fuel tank should be minimized to reduce the duration of fire. Adequate fire fighting equipment shall be provided, inspected and replaced periodically (e.g. fire extinguishers).	To reduce the risk during explosives transport	Contractor	Works areas of which explosives would be used	Construction stage	Dangerous Goods Ordinance	• N/A
\$9.18	Н8	The driver and his assistant should be physically healthy, experienced and have good safe driving records. The driver should hold a proper driving licence for the approved transport truck. Dedicated training programme and regular road safety briefing	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		sessions/ workshops should be provided to enhance their safe driving attitude and practice. Smoking should be strictly prohibited.						
S9.18	H9	Emergency response plans in case of road accident should be prepared and implemented. The driver and his assistant should be familiar with the emergency procedures including evacuation, and proper communication/ fire-fighting equipment should be provided to the driver and his assistant.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
S9.18	H10	Close liaison and communication among Mines Division, Contractors for transport of explosives, and working staff of the blasting should be established. In case of any change of work schedule leading to cancellation or variation of explosives required, relevant parties should be informed in time to avoid unused explosives at the work sites.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
\$9.18	H11	Close liaison and communication with Fire Services Department should be established to reduce the accidental detonation escalated from a fire. The contractors for transport of explosives should use the preferred transport routes as far as practicable.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
\$9.18	H12	Contingency plan should be prepared for transport of explosives under severe weather conditions such as rainstorms and thunderstorms.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S9.18	H13	For explosive transport, all packages of explosives on the truck should be properly stored in the truck compartment as required. Packaging of the explosives should remain intact (i.e. damage free) until they are transferred to the blasting site.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
S9.18	H14	Availability of a parking space should be ensured before commencement of transport of explosives. Location for loading and unloading of explosives should be as close as possible to the shaft. No hot work should be performed in the vicinity during the time of loading and unloading.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
S9.18	H22	It is recommended to explore to minimize the use of the cartridged emulsion explosives and maximize the use of bulk emulsion explosive as far as practicable.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
S9.18	H24	It is recommended to explore to use smaller explosive charges such as 'cast boosters' or 'mini-cast booster' instead of cartridged emulsion as primers for bulk emulsion. This option reduces the quantity of explosives required for transportation for the sections where bulk emulsion will be used.	To reduce the risk during explosives transport	Contractor	Works areas at which explosives would be used	Construction stage	-	• N/A
			Lan	dscape & Visual				
S10.10.1 Table 10.11	LV3	Good Site Management Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.	Minimize visual impact	Contractor	Within Project site	Construction stage	-	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 Construction plant and building material shall be orderly and carefully stored in order to create a neat and tidy visual appearance. 						
S10.10.1 Table 10.11	LV4	 Screen Hoarding Decorative screen hoarding should be erected to screen the public from the construction area. It should be designed to be compatible with the existing urban context. 	Minimize visual impact	Contractor	Within Project site	Construction stage	-	Implemented
S10.10.1 Table 10.11	LV5	Lighting Control during Construction All lighting in the construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residencies and GIC. The Contractor shall consider other security measures, which shall minimize the visual impacts.	Minimize visual impact	Contractor	Within Project site	Construction stage	-	Implemented
S10.10.1 Table 10.11	LV6	Erosion Control The potential for soil erosion shall be reduced by minimizing the extent of vegetation disturbance on site and by providing a protective cover over newly exposed soil.	Minimize landscape impact	Contractor	Within Project site	Construction stage	-	• N/A
S10.10.1 Table 10.11	LV7	Tree Protection & Preservation ■ Carefully protected during construction. Tree protection measures will be detailed at the Tree Removal Application stage and plans submitted to the relevant Government Department for approval in due course in accordance with ETWB TC no. 3/2006.	Minimize landscape and visual impact	Contractor	Within Project site	Construction stage	• 'Guidelines for Tree Risk Management and Assessment Arrangement on an Area Basis and on a Tree Basis', Greening,	 Implemented, deficiency rectified after observation


EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
\$10.10.1 Table 10.11	LV8	Tree Transplantation • For trees unavoidably affected by the Project that have to be removed, where practical transplantation will be chosen as the top priority method of removal. If this is not possible or practical compensatory planting will be provided for trees unavoidably felled (See LV10). For trees unavoidably affected by the Project works that are transplanted, transplantation must be carried out in accordance with ETWB TCW 2/2004 and 3/2006.	Minimize landscape and visual impact	Contractor	Within Project site and designated off-site locations	Prior to Construction stage	Landscape and Tree Management (GLTM) Section, DEVB Latest recommende d horticultural practices from GLTM Section, DEVB ETWB TCW 3/2006 Latest recommende d horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DEVB	• N/A

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
							2/2004	
S10.10.1 Table 10.11	LV9	 Compensatory Planting For trees unavoidably affected by the Project that have to be removed, where practical transportation will be chosen as the top priority method of removal but if this is not possible or practical compensatory planting will be provided for trees unavoidably felled. All felled trees shall be compensated for by planting trees to the satisfaction of relevant Government projects. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006. Compensatory tree planting may be incorporated into public open spaces and along roadside amenity areas affected by the construction works and therefore be part of the bigger wider planting plans. Onsite compensation planting is preferred but if necessary, additional receptor sites outside the Works Area shall be agreed separately with Government during the Tree Felling Application process. 	Minimize visual impact and also enhance landscape	Contractor	Within Project site	Construction stage	ETWB TCW 3/2006 Latest recommende d horticultural practices from Greening, Landscape and Tree Management (GLTM) Section, DEVB ETWB TCW 2/2004	• N/A
			Cultural Heritage	Impact (Construct	on Phase)			

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
S11.4.4	CH1	The contractor should be alerted during the construction on the possibility of locating archaeological remains and as a precautionary measure, AMO shall be informed immediately in case of discovery of antiquities or supposed antiquities in the subject sites.	To preserve any cultural heritage items which may be removed and damaged by the excavation	Contractor	During construction works for cut and cover tunnels	Construction stage	AMOs requirements	Implemented
S12.6.1	CH3	 Protective covering should be provided for the buildings in the form of plastic sheeting; Buffer zones should be provided between the construction works and the external walls of the buildings and should be as large as site restrictions allow and be marked out by temporary fencing or hoarding; An underpinning scheme is required to transfer the existing column loadings to a deeper rock stratum. The supporting system includes cutting the existing ground floor slab to expose the existing pile caps and then construct transfer beams at both sides of the pile caps. The transfer beams will tie up with the existing caps. Loadings of the transfer beams will be transferred to the rock socket piles installed at the two ends of the beams; The AAA settlement and tilting limit should be 6/8/10 mm and1/2000, 1/1500 and 1/1000; Monitoring of vibration levels will be undertaken during the construction phase and the Alert, Alarm and Action (AAA) vibration limit will be set at 5/6/7.5 mm/s. The monitoring proposal should be sent to AMO for comment;. 	Protect the building from damage from construction works	Contractor	Yau Ma Tei Police Station (Old Wing) (CKR-01)	Prior to commencement of and during the construction phase	Guidelines for Cultural Heritage Impact Assessment EIAO-TM Annex 10 and Annex 19 AMO Proposed Vibration Limits	• Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status
		 Regular site inspections and monitoring works will be carried out by the contractor and the monitoring results will be submitted to the resident site staff of HyD to ensure compliance. 						
\$12.6.1		 Adopting diaphragm wall construction method; Grout curtain should be provided in front of the building; Recharging system should be installed as a contingency measure to mitigate the fluctuation of water table; the AAA settlement and tilting limit should be 6/8/10 mm and 1/2000, 1/1500 and 1/1000; Monitoring of vibration levels will be undertaken during the construction phase and the Alert, Alarm and Action (AAA) vibration limit will be set at 5/6/7.5 mm/s. The monitoring proposal should be sent to AMO for comment;. Regular site inspections and monitoring works will be carried out by the contractor and the monitoring results will be submitted to the resident site staff of HyD to ensure compliance. 	Protect the building from damage from construction works	Contractor	Yau Ma Tei Police Station (Old Wing) (CKR-01)	Prior to commencement of and during the construction phase	Guidelines for Cultural Heritage Impact Assessment EIAO-TM Annex 10 and Annex 19 AMO Proposed Vibration Limits	• Implemented
S12.6.1 Table 12.2		 The Alert, Alarm and Action (AAA) vibration limit will be set at 3/4/5 mm/s and a condition survey shall be carried out by the project proponent prior to the construction phase to confirm this assessment Vibration monitoring of the structure shall be employed during the construction phase to ensure that the level is not exceeded. The monitoring proposal should be sent to AMO for comment. 	Protect the building from damage from construction works	Contractor	Tin Hau Temple (CKR- 02)	Prior to commencement of and during the construction phase	Guidelines for Cultural Heritage Impact Assessment EIAO-TM Annex 10 and Annex 19 AMO	Implemented

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommende d Measures & Main Concerns to address	Implementation Agent	Location / Timing	Implementation Stage	Requirements and/ or standards to be achieved	Implementation Status		
							Proposed Vibration Limits			
	EM&A Project									
S13.2	EM1	An Independent Environmental Checker needs to be employed as per the EM&A Manual	Control EM&A Performance	Highways Department	All construction sites	Construction stage	• EIAO Guidance Note No. 4/2010 • TM-EIAO	Implemented		
S13.2-13.4	EM2	 An Environmental Team needs to be employed as per the EM&A Manual; Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures; An environmental impact monitoring needs to be implemented by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with. 	Perform environmental monitoring & auditing	Highways Department/ Contractor	All construction sites	Construction stage	• EIAO Guidance Note No. 4/2010 • TM-EIAO	Implemented		



		Imp	act Monitoring Schedule for Y	MTE		
			Nov-22			
Sun	Mon	Tue	Wed	Thur	Fri	Sat
our .	11011	1	2	3	4	5
		Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A				
6	7	8	9	10	11	12
	Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A					Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A
13	14	15	16	17	18	19
					Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A	
20	21	22	23	24	25	26
				Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A		
27	28	29	30			
			Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A			

Contract No. HY/2014/08
Environmental Monitoring & Auditing

Appendix H
Calibration Certificates
(Air Monitoring)







Tel.: (852) 2698 6833 Fax: (852) 2698 9383

Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Verification Test Date: 27-Mar-22 to 3-Apr-22

 Next Verification Test Date:
 4-Apr-23

 Unit-under-Test- Model No.
 Sibata LD-5R

 Unit-under-Test Serial No.
 0Z4545

 Our Report Refrence No.
 RPT-22-HVS-0006

Standard Equipment Information		
Varification Equipment Type	Tisch's	TSP Tish HVS
Verification Equipment Type Standard Equipment Model No. Equipment serial no.	HVS	Calibrator
Standard Equipment Model No.	TE-517	0X TE-5028A
Equipment serial no.	MFC 1049	3702
Last Calibration Date	22-Mar	-22 3-Aug-21
Next Calibration Date	21-Jun-	-22 4-Aug-22

Verification	Date		Time		K-Factor	Counts/ Minute (R)	Total Counts	TSP Sample	Dust Concentration (ug/m3), (C)
Test No.		Start-time	End-time	Elapsed Time (in min)	K-Factor (K=C/R)	x-axis (TC)	(TC)	ID No.	y axis
1	27/3/2022	4945.81	4949.09	196.80	0.00078	64	12661	R220486/1	50
2	27/3/2022	4949.09	4952.83	224.40	0.00078	68	15259	R220486/2	53
3	27/3/2022	4952.83	4956.42	215.40	0.00075	63	13498	R220486/3	47
4	3/4/2022	4991.80	4995.40	216.00	0.00047	48	10296	R220538/1	22
5	3/4/2022	4995.40	4998.79	203.40	0.00045	52	10577	R220538/2	23
6	3/4/2022	4998.79	5002.26	208.20	0.00065	57	11937	R220538/3	37
					0.00065		·		

K-Factor to be inputted in LD-5R (corrected 1 decimal point):

0.6

By Linear Regression of y on x:

slope, mh= 1.7194 intercept,ch= -61.9131 *Correlation Coefficient,R= 0.9829

Verification Test Result: Strong Correlation, Results were accepted.


* If the Correlation Coefficient, R is <0.5. Checking and Re-

verification are required.

Verified By:

Field Supervisor

Date: 14-04-2022











Sibata LD-5R K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Verification Test Date: 27-Mar-22 to 3-Apr-22

Next Verification Test Date: 4-Apr-23
Unit-under-Test- Model No. Sibata LD-5R
Unit-under-Test Serial No. 992820
Our Report Refrence No. RPT-22-HVS-0004

Standard Equipment Information			
Verification Equipment Type		Tisch's TSP	Tish HVS
vernication Equipment Type		HVS	Calibrator
Standard Equipment Model No.		TE-5170X	TE-5028A
Equipment serial no.	MFC	1049	3702
Last Calibration Date		22-Mar-22	3-Aug-21
Next Calibration Date		21-Jun-22	4-Aug-22

Verification	Date		Time		K-Factor	Counts/ Minute (R)	Total Counts	TSP Sample	Dust Concentration (ug/m3), (C)
Test No.		Start-time	End-time	Elapsed Time (in min)	K-Factor (K=C/R)	x-axis	(TC)	ID No.	y axis
1	27/3/2022	4945.81	4949.09	196.80	0.00083	61	12005	R220486/1	50
2	27/3/2022	4949.09	4952.83	224.40	0.00082	65	14586	R220486/2	53
3	27/3/2022	4952.83	4956.42	215.40	0.00081	58	12493	R220486/3	47
4	3/4/2022	4991.80	4995.40	216.00	0.00047	48	10296	R220538/1	22
5	3/4/2022	4995.40	4998.79	203.40	0.00047	50	10102	R220538/2	23
6	3/4/2022	4998.79	5002.26	208.20	0.00067	56	11590	R220538/3	37
					0.00068				

K-Factor to be inputted in LD-5R (corrected 1 decimal point):

0.7

By Linear Regression of y on x:

slope, mh= 2.0047 intercept,ch= -73.6384


*Correlation Coefficient,R= 0.9763

Verification Test Result: Strong Correlation, Results were accepted.

* If the Correlation Coefficient, R is <0.5. Checking and Reverification are required.

Verified By:

Date: 14-04-2022









Tel.: (852) 2698 6833

PC-3A(E) K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Verification Test Date: 27-Mar-22 to 3-Apr-22

 Next Verification Test Date:
 4-Apr-23

 Unit-under-Test- Model No.
 PC-3A(E)

 Unit-under-Test Serial No.
 JC2002224

 Our Report Refrence No.
 RPT-22-HVS-0010

Standard Equipment Information			
Verification Equipment Type		Tisch's TSP	Tish HVS
		HVS	Calibrator
Standard Equipment Model No.		TE-5170X	TE-5028A
Equipment serial no.	MFC	1049	3702
Last Calibration Date		22-Mar-22	3-Aug-21
Next Calibration Date		21-Jun-22	4-Aug-22

Verification	Date		Time		K-Factor	Counts/ Minute (R)	Total Counts	TSP Sample	Dust Concentration (ug/m3), (C)
Test No.		Start-time	End-time	Elapsed Time (in min)	K-Factor (K=C/R)	x-axis	(TC)	ID No.	y axis
1	27/3/2022	4945.81	4949.09	196.80	0.00082	62	12136	R220486/1	50
2	27/3/2022	4949.09	4952.83	224.40	0.00082	65	14661	R220486/2	53
3	27/3/2022	4952.83	4956.42	215.40	0.00078	61	13068	R220486/3	47
4	3/4/2022	4991.80	4995.40	216.00	0.00048	47	10080	R220538/1	22
5	3/4/2022	4995.40	4998.79	203.40	0.00042	55	11187	R220538/2	23
6	3/4/2022	4998.79	5002.26	208.20	0.00064	58	12076	R220538/3	37
		•			0.00066		•		

K-Factor to be inputted in LD-5R (corrected 1 decimal point):

0.7

By Linear Regression of y on x:

slope, mh= 1.9032 intercept,ch= -71.2168 *Correlation Coefficient,R= 0.9103

Verification Test Result: <u>Strong Correlation, Results were accepted.</u>


 $\ensuremath{^{*}}$ If the Correlation Coefficient, R is <0.5. Checking and Re-

verification are required.

Verified By:

Field Supervisor

Date: <u>14-04-2022</u>









Tel.: (852) 2698 6833

PC-3A(E) K-Factor Verification Test by Total Suspended Particulates HVS Test Report

Verification Test Date: 27-Mar-22 to 3-Apr-22

 Next Verification Test Date:
 4-Apr-23

 Unit-under-Test- Model No.
 PC-3A(E)

 Unit-under-Test Serial No.
 JC2002225

 Our Report Refrence No.
 RPT-22-HVS-0011

Standard Equipment Information				
ferification Equipment Type standard Equipment Model No. squipment serial no. ast Calibration Date	Т	isch's TSP	Tish HVS	_
vernication Equipment Type		HVS	Calibrator	
Standard Equipment Model No.	-	TE-5170X	TE-5028A	
Equipment serial no.	MFC	1049	3702	
Last Calibration Date	2	22-Mar-22	3-Aug-21	
Next Calibration Date	:	21-Jun-22	4-Aug-22	

Verification	Date		Time		K-Factor	Counts/ Minute (R)	Total Counts	TSP Sample	Dust Concentration (ug/m3), (C)
Test No.		Start-time	End-time	Elapsed Time (in min)	K-Factor (K=C/R)	x-axis	(TC)	ID No.	y axis
1	27/3/2022	4945.81	4949.09	196.80	0.00078	64	12661	R220486/1	50
2	27/3/2022	4949.09	4952.83	224.40	0.00080	67	14960	R220486/2	53
3	27/3/2022	4952.83	4956.42	215.40	0.00076	62	13427	R220486/3	47
4	3/4/2022	4991.80	4995.40	216.00	0.00042	53	11448	R220538/1	22
5	3/4/2022	4995.40	4998.79	203.40	0.00042	55	11187	R220538/2	23
6	3/4/2022	4998.79	5002.26	208.20	0.00064	58	12006	R220538/3	37
			•	•	0.00064				

K-Factor to be inputted in LD-5R (corrected 1 decimal point):

0.6

By Linear Regression of y on x:

slope, mh= 2.4515 intercept,ch= -107.7256 *Correlation Coefficient,R= 0.9802

Verification Test Result: Strong Correlation, Results were accepted.


 $\ensuremath{^{*}}$ If the Correlation Coefficient, R is <0.5. Checking and Re-

verification are required.

Verified By:

Field Supervisor

Date: <u>14-04-2022</u>





RECALIBRATION DUE DATE:

June 28, 2023

Certificate of Calibration

Calibration Certification Information

Cal. Date: June 28, 2022

Rootsmeter 5/N: 438320

Ta: 296

°K

Operator: Jim Tisch

Pa: 755.1

mm Hg

Calibration Model #:	TE-5025A
----------------------	----------

Calibrator S/N: 3465

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4290	3.2	2.00
2	3	4	1	1.0130	6.4	4.00
3	5	6	1	0.9050	7.9	5.00
4	7	8	1	0.8590	8.8	5.50
5	9	10	1	0.7110	12.8	8.00

		Data Tabulat	tion		
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right) \left(\frac{Tstd}{Ta}\right)}$ (y-axis)	Va	Qa (x-axis)	√∆H(Ta/Pa)
0.9961	0.6970	1.4144	0.9958	0.6968	0.8854
0.9918	0.9791	2.0003	0.9915	0.9788	1.2522
0.9899	1.0938	2.2364	0.9895	1.0934	1.4000
0.9887	1.1509	2.3456	0.9883	1.1506	1.4683
0.9834	1.3831	2.8289	0.9830	1.3826	1.7708
resone !	m=	2.05924		m=	1.28946
QSTD	b=	-0.01929	QA	b=	-0.01207
	r=	0.99998		r=	0.99998

Calculati	ons
Vstd= ΔVol((Pa-ΔP)/Pstd)(Tstd/Ta)	Va= ΔVol((Pa-ΔP)/Pa)
Qstd= Vstd/∆Time	Qa= Va/ΔTime
For subsequent flow r	ate calculations:
$Qstd= 1/m \left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) \cdot b$	Qa= $1/m\left(\left(\sqrt{\Delta H(Ta/Pa)}\right)-b\right)$

	Standard Conditions
Tstd:	298.15 °K
Pstd:	760 mm Hg
	Key
ΔH: calibrator	manometer reading (in H2O)
	er manometer reading (mm Hg)
Ta: actual abs	olute temperature (°K)
Pa: actual bar	ometric pressure (mm Hg)
b: intercept	
m: slope	

RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Tisch Environmental, Inc. 145 South Miami Avenue Village of Cleves, OH 45002

www.tisch-env.com TOLL FREE: (877)263-7610 FAX: (513)467-9009

創新科儀有限公司

I	HIVOL	SAMPLER	CALIB	RATION	DATA SHE	ET (TSP))
			Site	Informatio	on		
	YMT	Catholic					
Location:	Prima	ry School	Site ID	: W-A1	Date:	01 - Nov	-2022
Serial No:		1084	Model:	TE-5170X	Operator:	An	dy
			Amhie	nt Conditi	On		
Corrected 1	Pressure	(mm Hg):	764.8	Temperatur		300).9
		(871		1	. (l	
			Calibr	ation Orif	ice		
Model:			1	ΓΕ-5025A	Slope:	1.28	946
Serial No.	•			3465	Intercept:	-0.01	207
Calibration	n Due Da	te:	2	8-Jun-23	Corr. Coeff	0.99	998
			•		•	•	
			Calit	oration Dat	a		
Plate or		In,H20	Qa, X-Axis		I, CFM	IC, Y-Axis	
Test #		(in)	(1	m3/min)	(chart)	(corrected)	
1		1.20		0.858	38.0	37.94	
2		2.16		1.147	39.1	39.04	
3		3.02		1.355	39.9	39.84	
4		3.67		1.493	40.5	40.44	
5		4.21		1.598	40.8	40.74	
Sampler Calibta	ation Relatio	onship (Qa on x-ax	is, IC on y-ax	ris)			
m=		3.8343	b=	34.6505		Corr. Coeff=	0.9994
Sam	pler set poi	nt(SSP)	39	CFM			
		,			_		
			Ca	lculations			
		std)(Tstd/Ta))-b]		m = sampler s	•		
IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]			<pre>b = sampler intercept l = chart response</pre>				
Qstd = standard flow rate			Tav = average temperature				
IC = corrected chart response			Pav = average pressure				
I = actual chart response				0 .	•		
n = calibrator	Ostd slope						
= calibrator							
	•	ring calibration (
a = actual pre	ssure durin	g calibration (mm	Hg)				
std = 298 deg	K						
std = 760 mm	Hg						

Date:

1-Nov-22

Checked by:

For subsequent calculation of sampler flow: (1.21*m+b)/[Sqrt(298/Tav)(Pav/760)]

創新科儀有限公司

HIVOL SAMPLER CALIBRATION DATA SHEET (TSP)

a	т с			•	
Site	Info	rma	t	1 on	

Location:	Man Cheong Buil	ding Site ID:	₩-A6	Date:	01 - Nov - 2022
Serial No:	1050	Mode1:	TE-5170X	Operator:	Andy

Ambient Condition

Corrected Pressure (mm Hg):	764.8	Temperature (deg K):	300.9
-----------------------------	-------	----------------------	-------

Calibration Orifice

Model:	TE-5025A	Slope:	1.28946
Serial No.:	3465	Intercept:	-0.01207
Calibration Due Date:	28-Jun-23	Corr. Coeff:	0.99998

Calibration Data

Plate or	In,H20	Qa, X-Axis	I, CFM	IC, Y-Axis
Test #	(in)	(m3/min)	(chart)	(corrected)
1	1.23	0.868	37.2	37.14
2	1.91	1.079	38.1	38.04
3	2.23	1.166	38.4	38.34
4	3.84	1.527	39.7	39.64
5	4.10	1.577	39.9	39.84

Sampler Calibtatio	n Relationship (Qa on x-axis	s, IC on y-a	xis)		
m=	3.7389	b=	33.9499	Corr. Coeff=	0.9993
Sample	er set point(SSP)	39	СЕМ		
		Ca	lculations.		
Qstd = 1/m[Sqrt(H)]	2O(Pa/Pstd)(Tstd/Ta))-b]		m = sampler slope		
IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]		b = sampler intercept		
			<pre>I = chart response</pre>		
Qstd = standard fl	ow rate		Tav = average temperature		
IC = corrected cha	rt response		Pav = average pressure		
I = actual chart res	sponse				
m = calibrator Qs	td slope				
b = calibrator Qst	d intercept				
Ta = actual temper	ature during calibration (d	eg K)			
Pa = actual pressu	re during calibration (mm	Hg)			
Tstd = 298 deg K					
Pstd = 760 mm Hg					
For subsequent ca	Iculation of sampler flow:				
(1.21*m+b)/[Sqrt(2	298/Tav)(Pav/760)]				
Checked by:	· h		Date:	1-No	v-22

1084

創新科儀有限公司

Serial No:

HIVOL SAMPLER CALIBRATION DATA SHEET (TSP)

Site Information						
	YMT Catholic					
Location:	Primary School	Site	ID:	₩-A1	Date:	16-Nov-2022

TE-5170X Operator:

Ambient Condition

Model:

Corrected Pressure (mm Hg):	762.0 Temperatu	re (deg K):	301.5

Calibration Orifice

Model:	TE-5025A	Slope:	1.28946
Serial No.:	3465	Intercept:	-0.01207
Calibration Due Date:	28-Jun-23	Corr. Coeff	0.99998

Calibration Data

Plate or	In,H20	Qa, X-Axis	I, CFM	IC, Y-Axis
Test #	(in)	(m3/min)	(chart)	(corrected)
1	1.97	1.093	37.3	37.13
2	2.38	1.200	37.7	37.53
3	3.04	1.356	38.3	38.13
4	3.59	1.472	38.8	38.63
5	4.04	1.561	39.1	38.93

Sampler Calibtation Relationship (Qa on x-axis, IC on y-axis)

Sampler Calibtatio	n Kelationship (Qa on x-axi:	s, ic on y-a	xis)		
m=	3.8770	b=	32.8883	Corr. Coeff=	0.9996
Sample	er set point(SSP)	38	CFM		
		Ca	lculations		
Qstd = 1/m[Sqrt(Hi	2O(Pa/Pstd)(Tstd/Ta))-b]		m = sampler slope		
IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]		b = sampler intercept		
			I = chart response		
Qstd = standard fl	ow rate		Tav = average temperature		
IC = corrected char	rt response		Pav = average pressure		
I = actual chart res	sponse				
m = calibrator Qs	td slope				
b = calibrator Qst	d intercept				
•	ature during calibration (d	0 ,			
Pa = actual pressu	re during calibration (mm	Hg)			
Tstd = 298 deg K					
Pstd = 760 mm Hg					
For subsequent ca	Iculation of sampler flow:				
(1.21*m+b)/[Sqrt(2	298/Tav)(Pav/760)]				
Checked by:	· h		Date:	16-No	ov-22

創新科儀有限公司

HIVOL SAMPLER CALIBRATION DATA SHEET (TSP)

α	•		т -	•			•
Ν.	1	tΑ	l n	† C	\ rm a	t	ion
v	1	ιU		1	, т ш а	· L	1011

Location:	Man Cheong Building	Site ID:	W -A6	Date:	16-Nov-2022
Serial No:	1050	Mode1:	TE-5170X	Operator:	Andy

Ambient Condition

G . 1 B . (II)	762.0	m	201 F
Corrected Pressure (mm Hg):	762.0	Temperature (deg K):	301.5

Calibration Orifice

Model:	TE-5025A	Slope:	1.28946
Serial No.:	3465	Intercept:	-0.01207
Calibration Due Date:	28-Jun-23	Corr. Coeff	0.99998

Calibration Data

Plate or	In,H20	Qa, X-Axis	I, CFM	IC, Y-Axis
Test #	(in)	(m3/min)	(chart)	(corrected)
1	1.23	0.866	37.9	37.73
2	2.16	1.144	38.7	38.53
3	3.18	1.386	39.5	39.32
4	3.72	1.498	39.8	39.62
5	4.12	1.576	40.1	39.92

Sampler Calibtation Rela	ationship (Qa on x-axis, IC on 3.0701	y-axis) b=	35.0524	Corr. Coeff=	0.9994
Sampler se	et point(SSP)	39	CFM		
		Cal	culations		
Qstd = 1/m[Sqrt(H2O(Pa	/Pstd)(Tstd/Ta))-b]		m = sampler slope		
IC = I[Sqrt(Pa/Pstd)(Tstd	/Ta)]		b = sampler intercept		
			I = chart response		
Qstd = standard flow ra	te		Tav = average temperature		
IC = corrected chart resp	oonse		Pav = average pressure		
I = actual chart response	e				
m = calibrator Qstd slo	pe				
b = calibrator Qstd inte	rcept				
Ta = actual temperature	during calibration (deg K)				
Pa = actual pressure dui	ring calibration (mm Hg)				
Tstd = 298 deg K					
Pstd = 760 mm Hg					
For subsequent calculat	ion of sampler flow:				

Date:

16-Nov-22

(1.21*m+b)/[Sqrt(298/Tav)(Pav/760)]

Checked by:

Environmental Monitoring & Auditing
A 11 T
Appendix I
Calibration Certificates (Noise)
Canonation Continuates (110150)

Contract No. HY/2014/08



Certificate of Calibration

for

Description:

Sound Level Meter

Manufacturer:

NTi Audio

Type No.:

XL2 (Serial No.: A2A-13548-E0)

Microphone:

ACO 7052 (Serial No.:73912)

Preamplifier:

NTi Audio M2211 MA220 (Serial No.:5735)

Submitted by:

Customer:

Acuity Sustainability Consulting Limited

Address:

Unit C, 11/F., Ford Glory Plaza, No. 37-39 Wing Hong Street,

Cheung Sha Wan, Kowloon

Upon receipt for calibration, the instrument was found to be:

✓ Within

☐ Outside

the allowable tolerance.

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 30 December 2021

Date of calibration: 3 January 2022

 Certified by:

Mr. Ng Yan Wa Laboratory Manager

Date of issue: 3 January 2022

Certificate No.: APJ21-132-CC001

AND NAR TESTING ASSOCIATION OF THE PROPERTY OF

Page 1 of 4

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong Tel: (852) 2668 3423 Fax:(852) 2668 6946



1. Calibration Precaution:

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

2. Calibration Conditions:

Air Temperature: 22.6 °C
Air Pressure: 1006 hPa
Relative Humidity: 53.6 %

3. Calibration Equipment:

	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV200041	HOKLAS

4. Calibration Results

Sound Pressure Level

Reference Sound Pressure Level

Sett	ing of U	nit-under-te	est (UUT)	Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq.	Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBA	SPL	Fast	94	1000	94.1	±0.4

Linearity

Setting of Unit-under-test (UUT)			App	Applied value		IEC 61672 Class 1	
Range, dB	Freq. V	Veighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
				94		94.1	Ref
30-130	dBA	SPL	Fast	104	1000	104.1	±0.3
				114		114.1	±0.3

Time Weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. W	eighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBA	SPL	Fast	94	1000	94.1	Ref
30-130	UDA	SFL	Slow	94	1000	94.1	±0.3

Certificate No.: APJ21-132-CC001

Page 2 of 4

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong Tel: (852) 2668 3423 Fax:(852) 2668 6946

Homepage: http://www.aa-lab.com

E-mail: inquiry@aa-lab.com



Frequency Response

Linear Response

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. We	eighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
					31.5	94.1	±2.0
					63	94.1	±1.5
					125	94.1	±1.5
					250	94.1	±1.4
30-130	dB	SPL	Fast	94	500	94.1	±1.4
					1000	94.1	Ref
					2000	94.5	±1.6
					4000	95.2	±1.6
					8000	94.6	+2.1; -3.1

A-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. W	eighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
					31.5	54.7	-39.4 ±2.0
					63	67.9	-26.2 ±1.5
					125	78.0	-16.1 ±1.5
					250	85.4	-8.6 ±1.4
30-130	dBA	SPL	Fast	94	500	90.9	-3.2 ±1.4
					1000	94.1	Ref
					2000	95.7	+1.2 ±1.6
		-			4000	96.2	+1.0±1.6
					8000	93.4	-1.1+2.1; -3.1

C-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. V	Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
					31.5	91.1	-3.0 ±2.0
					63	93.3	-0.8 ±1.5
					125	93.9	-0.2 ±1.5
					250	94.1	-0.0 ±1.4
30-130	dBC	SPL	Fast	94	500	94.2	-0.0 ±1.4
					1000	94.1	Ref
		1			2000	94.3	-0.2 ±1.6
					4000	94.4	-0.8 ±1.6
					8000	91.5	-3.0 +2.1: -3.1

Certificate No.: APJ21-132-CC001



Page 3 of 4

Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong Tel: (852) 2668 3423 Fax:(852) 2668 6946



5. Calibration Results Applied

The results apply to the particular unit-under-test only. All calibration points are within manufacture's specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.05
	63 Hz	± 0.05
	125 Hz	± 0.05
	250 Hz	± 0.05
	500 Hz	± 0.05
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	± 0.05
	8000 Hz	± 0.10
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

Note:

The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)*L shall not be liable for any loss or damage resulting from the use of the equipment.

Certificate No.: APJ21-132-CC001





Certificate of Calibration

for

Description:

Sound Level Meter

Manufacturer:

Lutron

Type No.:

SL-4033SD (Serial No.: I.491835)

Submitted by:

Customer:

Acuity Sustainability Consulting Limited

Address:

Unit C, 11/F., Ford Glory Plaza, No. 37-39 Wing Hong Street,

Cheung Sha Wan, Kowloon

Upon receipt for calibration, the instrument was found to be:

☑ Within (A-Weighting, 31.5Hz to 2000Hz)

☐ Outside

the allowable tolerance.

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 30 December 2021 Date of calibration: 3 January 2022

Calibrated by:

Calibration Technician

Certified by:

Mr. Ng Yan Wa Laboratory Manager

Date of issue: 3 January 2022

Certificate No.: APJ21-132-CC002

Page 1 of 3



1. Calibration Precaution:

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

2. Calibration Conditions:

Air Temperature: $22.6\,^{\circ}\text{C}$ Air Pressure: $1006\,\text{hPa}$ Relative Humidity: $53.6\,\%$

3. Calibration Equipment:

	Type	Serial No.	Calibration Report Number	Traceable to	
Multifunction Calibrator	B&K 4226	2288467	AV200041	HOKLAS	

4. Calibration Results

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)		Applied value		UUT Reading,	IEC 61672 Class 1		
Range, dB	Freq. V	Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBA	SPL	Fast	94	1000	94.0	±0.4

Linearity

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. V	Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
				94		94.0	Ref
30-130	dBA	SPL	Fast	104	1000	104.1	±0.3
				114		113.8	±0.3

Time Weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. W	eighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
30-130	dBA	SPL	Fast	94	1000	94.0	Ref
30-130	UDA	SFL	Slow	94	1000	94.0	±0.3

Certificate No.: APJ21-132-CC002

A Page 2 of 3

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street , Fo Tan, Shatin, N.T., Hong Kong
Tel: (852) 2668 3423 Fax: (852) 2668 6946



Frequency Response

A-weighting

Setting of Unit-under-test (UUT)			Applied value		UUT Reading,	IEC 61672 Class 1	
Range, dB	Freq. V	Veighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB
					31.5	55.4	-39.4 ±2.0
					63	67.9	-26.2 ±1.5
					125	77.9	-16.1 ±1.5
30-130	dBA	SPL	Fast	94	250	85.3	-8.6 ±1.4
					500	91.0	-3.2 ±1.4
					1000	94.0	Ref
					2000	94.4	+1.2 ±1.6

5. Calibration Results Applied

The results apply to the particular unit-under-test only. All calibration points are within manufacture's specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.05
	63 Hz	± 0.10
	125 Hz	± 0.05
	250 Hz	± 0.05
	500 Hz	± 0.05
	1000 Hz	± 0.05
	2000 Hz	± 0.05
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

Note:

The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)*L shall not be liable for any loss or damage resulting from the use of the equipment.

Certificate No.: APJ21-132-CC002



Room 422,Leader Industrial Centre,57-59 Au Pui Wan Street ,Fo Tan, Shatin,N.T.,Hong Kong
Tel: (852) 2668 3423 Fax:(852) 2668 6946



CALIBRATION CERTIFICATE

Certificate Informat	ion									
Date of Issue	11-Feb-2022		Certificate Numb	er MLCN220284S						
Customer Informati	on									
Company Name Address	Unit E, 12/F., F Nos. 37-39 Wir	Acuity Sustainability Consulting Limited Unit E, 12/F., Ford Glory Plaza, Nos. 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon, HK								
Equipment-under-T	est (EUT)		West State of the							
Description Manufacturer Model Number Serial Number Equipment Number	Sound Level Ca Rion NC-74 34504770	alibrator								
Calibration Particul	ar									
Date of Calibration Calibration Equipment	,	11-Feb-2022 4231(MLTE008) / AV200063 / 23-Jun-23 1357(MLTE190) / MLEC21/05/02 / 26-May-22								
Calibration Procedure	MLCG00, MLC	CG15								
Calibration Conditions	Laboratory EUT	Temperature Relative Humidity Stabilizing Time Warm-up Time Power Supply	23 °C ± 5 °C 55% ± 25% Over 3 hours Not applicable Internal battery							
Calibration Results		were detailed in the cult was within EUT spo	, .							
Approved By & Date		//-								
Ct. 1		- 01	K.O. Lo	11-Feb-2022						
	on Certificate only r	elate to the values measure	nternational standards. ed at the time of the calibration and the							

Page 1 of 2

not include allowance for the EUT long term drift, variation with environmental changes, vibration and shock during transportation,

MaxLab Calibration Centre Limited shall not be liable for any loss or damage resulting from the use of the EUT.
 The copy of this Certificate is owned by MaxLab Calibration Centre Limited. No part of this Certificate may be reproduced without the prior written approval of MaxLab Calibration Centre Limited.

overloading, mishandling, misuse, and the capacity of any other laboratory to repeat the measurement.

萬 儀 校 正 中 心 有 限 公 司 MaxLab Calibration Centre Limited 香港新界葵涌華星街 16-18 號保盈工業大廈 9 樓 B 室 Unit B, 9/F., Boldwin Industrial Bldg., 16-18 Wah Sing Street, Kwai Chung, N.T., Hong Kong Tel: (852) 2116 1380 Fax: (852) 2264 6480 Email: info@maxlab.com.hk



Certificate No. MLCN220284S

Calibration Data							
EUT Setting	Standard Reading	EUT Error from Setting	Calibration Uncertainty	EUT Specification			
94 dB	94.0 dB	0.0 dB	0.20 dB	± 0.3 dB			

- END -

Calibrated By: Date :

Dan


11-Feb-22

Checked By:

Date:

K.O. Lo 11-Feb-22

Page 2 of 2





Hong Kong Accreditation Service 香港認可處

Certificate of Accreditation 認可證書

This is to certify that 特此證明

ACUMEN LABORATORY AND TESTING LIMITED

浩科檢測中心有限公司

Flat/Rm D, 12/F, Ford Glory Plaza, Nos. 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon, Hong Kong

香港九龍長沙灣永康街37-39號福源廣場12樓D室

is accredited by the Hong Kong Accreditation Service (HKAS) to ISO/IEC 17025:2017 for performing specific laboratory activities as listed in the scope of accreditation within the test category of 獲香港認可處根據ISO/IEC 17025:2017認可 進行戰於認可範圍內下述測試類別中的指定實驗所活動

Environmental Testing

環境測試

This accreditation to ISO/IEC 17025:2017 demonstrates technical competence for a defined scope and the implementation of a management system relevant to laboratory operation (see joint IAF-ILAC-ISO Communiqué).

此项 ISO/IEC 17025:2017 的認可資格證明此實驗所具備指定範疇內所須的技術能力並 實施一套與實驗所運作相關的管理關系 (見國際認可結婚・國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of HKAS is affixed hereto by the authority of the HKAS Executive 現經香港認可處執行機關授權在此蓋上香港認可慮的印章

SHUM Wai-leung, Executive Administrator

執行幹事 沈偉良

Issue Date: 15 November 2021

簽發日期:二零二一年十一月十五日

Registration Number : HOKLAS 241

Date of First Registration: 16 July 2014 首次註冊日期:二零一四年七月十六日

This certificate is issued subject to the terms and conditions laid down by HKAS 本體書級照香港認可盡訂立的條款及條件發出

L002316



Hong Kong Accreditation Service 香港認可處

Certificate of Accreditation

認可證書

This is to certify that 特此間明

ALS TECHNICHEM (HK) PTY LIMITED

11/F, Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong 香港新界葵涌永業街1-3號忠信針織中心11樓

is accredited by the Hong Kong Accreditation Service (HKAS) to ISO/IEC 17025:2017 for performing specific laboratory activities as listed in the scope of accreditation within the test category of 獲香港認可處根據ISO/IEC 17025:2017認可 進行戰於認可範圍內下述測試類別中的指定實驗所活動

Environmental Testing

環境測試

This accreditation to ISO/IEC 17025:2017 demonstrates technical competence for a defined scope and the implementation of a management system relevant to isboratory operation (see joint IAF-ILAC-ISO Communiqué).

此項 ISO/IEC 17025:2017 的認可資格證明此實驗所具備指定範疇內所須的技術能力並 實施一套與實驗所運作相關的管理體系 (見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of HKAS is affixed hereto by the authority of the HKAS Executive 現經香港認可處執行機關授權在此蓋上香港認可處的印章

SHUM Wai-leung, Executive Administrator

執行幹事 沈偉良

Issue Date : 28 February 2020

签發日期:二零二零年二月二十八日

Registration Number : HOKLAS 066

註冊號碼:




Date of First Registration: 15 September 1995 首次註冊日期:一九九五年九月十五日


This certificate is issued subject to the terms and conditions laid down by HKAS. 本證書按照香港認可處訂立的條款及條件發出

L001934

Contract No. HY/2014/08
Environmental Monitoring & Auditing

Appendix K
Location Plan of Noise and Air Quality
Monitoring Station

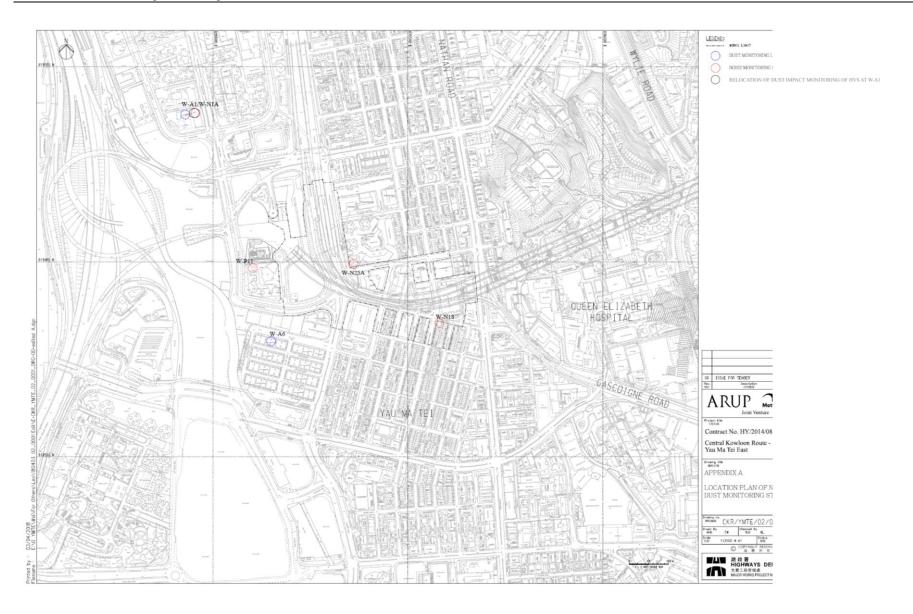



Location: Yau Ma Tei Catholic Primary School (Hoi Wang Road) (W-A1)

Monitoring date: 1, 7, 12, 18, 24 and 30 November 2022

Parameter: TSP 1-hour Other Factors Nearby traffic

	1-hour TSP (μg/m³)										
Date	Weather	Start Time	1 st Hour (μg/m³)	2 nd Hour (μg/m³)	3 rd Hour (μg/m³)						
01/11/2022	Fine	10:09	46	51	55						
07/11/2022	Fine	9:37	53	66	61						
12/11/2022	Fine	9:34	55	58	54						
18/11/2022	Fine	9:01	52	56	55						
24/11/2022	Cloudy	12:45	59	64	66						
30/11/2022	Fine 12:47		51	62	60						
Mini	mum: 46 μg/m ³	3		Maximum: 66 μg/m ³							

Location:

Man Cheong Building (W-A6) 1, 7, 12, 18, 24 and 30 November 2022 Monitoring date:

TSP 1-hour Parameter: Nearby traffic Other Factors

	1-hour TSP (μg/m³)											
Date	Weather	Start Time	1 st Hour (μg/m³)	2 nd Hour (μg/m³)	3 rd Hour (μg/m³)							
01/11/2022	Fine	9:30	53	59	62							
07/11/2022	Fine	11:14	64	70	69							
12/11/2022	Fine	10:31	61	67	74							
18/11/2022	Fine	9:46	60	68	72							
24/11/2022	Cloudy	13:44	68	74	70							
30/11/2022	Fine	9:45	54	66	67							
	Minimum: 53	μg/m ³		Maximum: 74 μg	g/m ³							

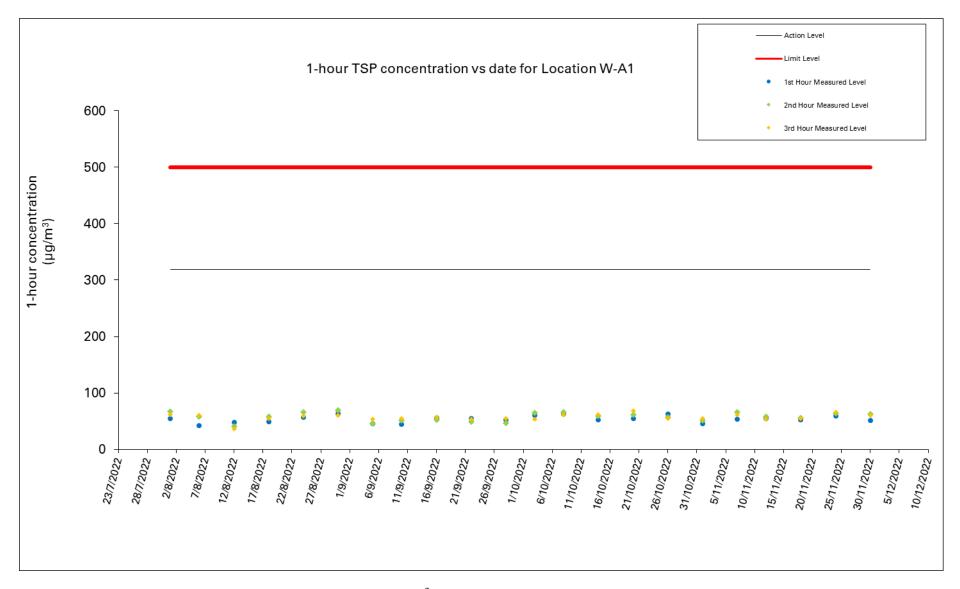


Figure 1: Graphical Illustration of Measured 1-hour TSP (μg/m³) Levels at W-A1

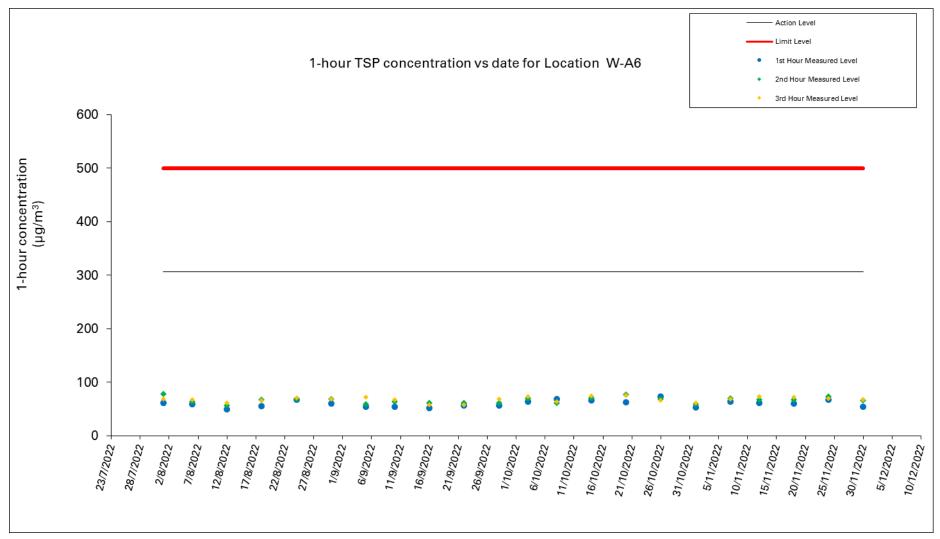


Figure 2: Graphical Illustration of Measured 1-hour TSP (μg/m³) Levels at W-A6

Yau Ma Tei Catholic Primary School (Hoi Wang Road) (W-A1) 1, 7, 12, 18, 24 and 30 November 2022 Location:

Monitoring date:

TSP 24-hour Parameter: Other Factors Nearby traffic

Date of Calibration:	1-Nov-22	Slope =	3.8343
Calibration due date:	16-Nov-22	Intercept =	34.6505
Date of Calibration:	16-Nov-22	Slope =	3.8770
Calibration due date:	1-Dec-22	Intercept =	32.8883

Start Date	Weather	Elapse Time		Chart Reading		Avg Air Temp	Avg Atmospheric Pressure	Flow Rate	Standard Air Volume	Filter Weight (g)		Particulate weight	Conc.		
	Condition	Initial	Final	Actual (min)	Min	Max	Avg	(°C)	(hPa)	(m³/min)	(m ³)	Initial	Final	(g)	$(\mu g/m^3)$
1/11/2022	Fine	7372.9	7396.9	1440.0	40	40	40.0	22.0	1008.2	1.40	2010	2.7622	2.8163	0.0541	27
7/11/2022	Fine	7396.9	7420.9	1440.0	38	40	39.0	21.5	1017.3	1.24	1779	2.7797	2.8202	0.0405	23
12/11/2022	Fine	7420.9	7444.9	1440.0	42	42	42.0	24.6	1015.3	1.95	2803	2.7774	2.8421	0.0647	23
18/11/2022	Fine	7445.2	7469.2	1440.0	38	40	39.0	24.6	1015.6	1.61	2313	2.7043	2.7495	0.0452	20
24/11/2022	Cloudy	7469.2	7493.2	1440.0	38	39	38.5	21.8	1015.2	1.52	2189	2.7668	2.7941	0.0273	12
30/11/2022	Fine	7493.2	7517.2	1440.0	39	39	39.0	22.8	1017.3	1.65	2382	2.7727	2.8070	0.0343	14
·										Maximum:	27	μg/m ³	Minimum:	12	μg/m ³

Location:

Man Cheong Building (W-A6) 1, 7, 12, 18, 24 and 30 November 2022 Monitoring date:

Parameter: TSP 24-hour Nearby traffic Other Factors

Date of Calibration:	1-Nov-22	Slope =	3.7389
Calibration due date:	16-Nov-22	Intercept =	33.9499
Date of Calibration:	16-Nov-22	Slope =	3.0701
Calibration due date:	1-Dec-22	Intercept =	35.0524

								campiation add date: 1-D		1 DCC 22	rcc 22 IIIIci		33.03E		
Start Date	Weather Condition	Elapse Time		Elapse Time Chart Reading			Avg Air Temp	Avg Atmospheric Pressure	Flow Rate	Standard Air Volume	Filter Weight (g)		Particulate weight	Conc.	
	Condition	Initial	Final	Actual (min)	Min	Max	Avg	(°C)	(hPa)	(m³/min)	(m ³)	Initial	Final	(g)	$(\mu g/m^3)$
1/11/2022	Fine	6961.3	6985.3	1440.00	48	48	48.0	22.0	1008.2	3.76	5412	2.7592	2.8386	0.0794	15
7/11/2022	Fine	6985.3	7009.3	1440.00	45	46	45.5	21.5	1017.3	3.21	4623	2.7868	2.8457	0.0589	13
12/11/2022	Fine	7009.3	7033.3	1440.00	34	38	36.0	24.6	1015.3	0.57	827	2.7773	2.845	0.0677	82
18/11/2022	Fine	7033.5	7057.5	1440.00	38	38	38.0	24.6	1015.6	1.00	1436	2.7136	2.8174	0.1038	72
24/11/2022	Cloudy	7057.5	7081.5	1440.00	39	39	39.0	21.8	1015.2	1.38	1986	2.7426	2.7908	0.0482	24
30/11/2022	Fine	7081.5	7105.5	1440.00	46	52	49.0	22.8	1017.3	4.67	6719	2.7642	2.8366	0.0724	11
			-			•	•	•		Maximum:	82	μg/m ³	Minimum:	11	μg/m³

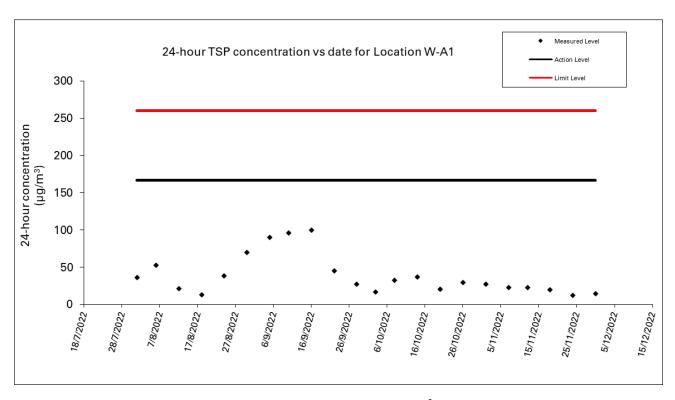


Figure 3: Graphical Illustration of Measured 24-hour TSP (μg/m³) Levels at W-A1


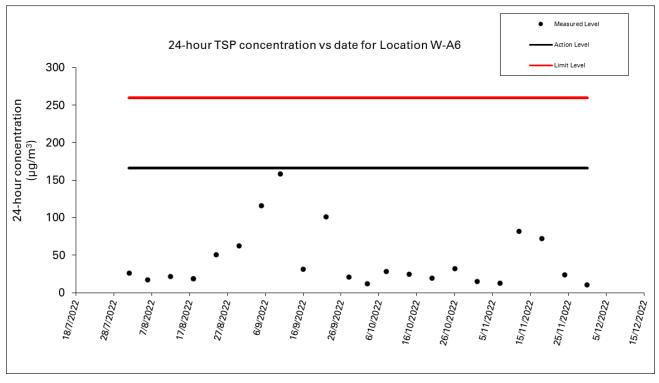



Figure 4: Graphical Illustration of Measured 24-hour TSP (μg/m³) Levels at W-A6

Wind direction data for 1, 2, 7, 8, 12, 13, 18, 19, 24, 25, 30 November and 1 December 2022








(於香港時間02/11/2022 23 時 40 分更新) (Updated at 23:40H on 02/11/2022)









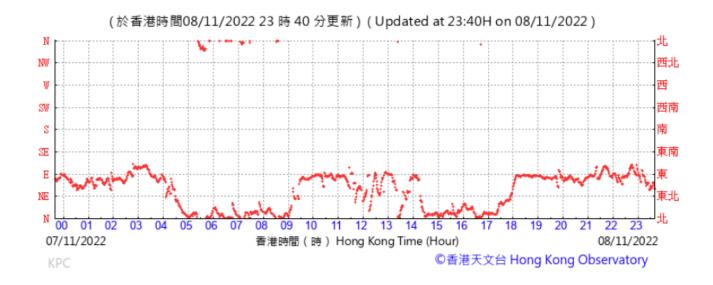

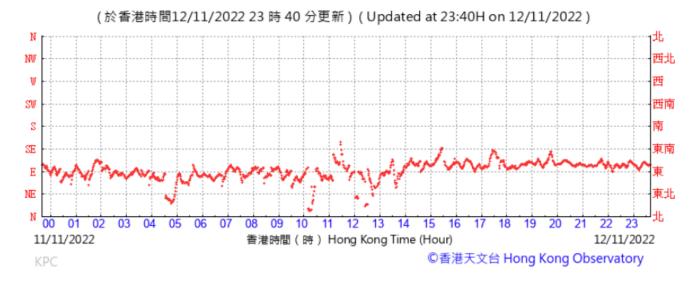

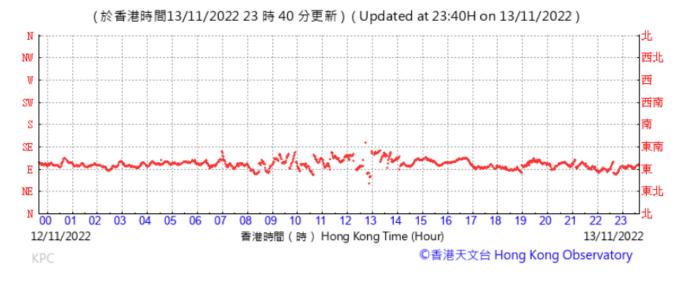


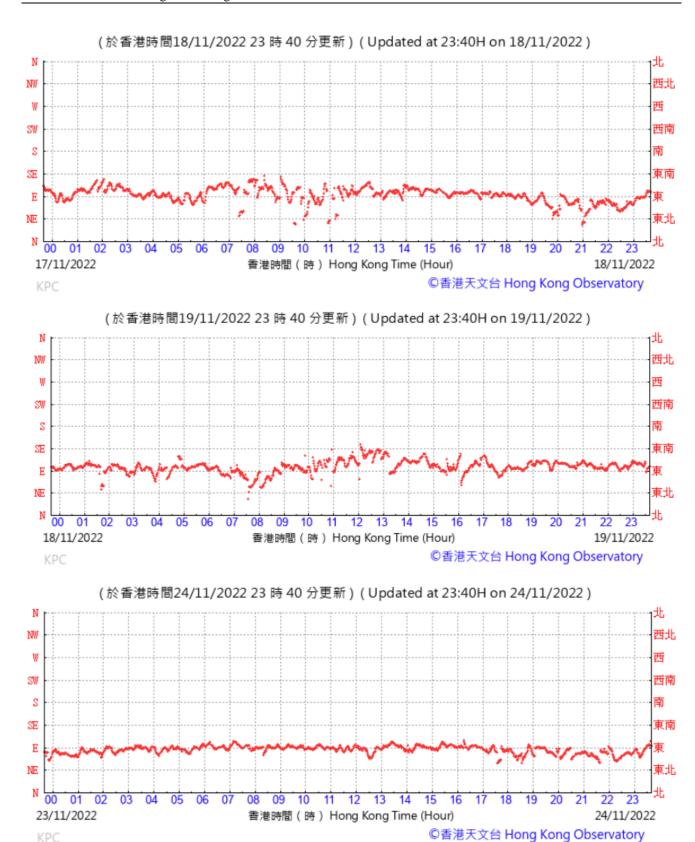


KPC







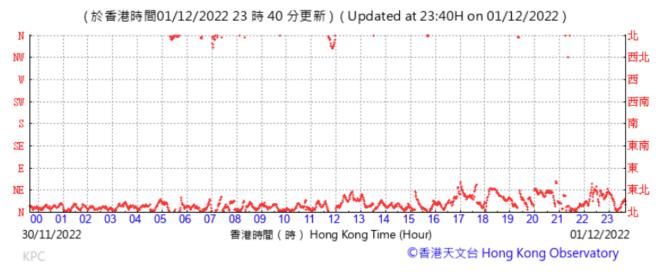

Wind speed data for 1, 2, 7, 8, 12, 13, 18, 19, 24, 25, 30 November and 1 December 2022

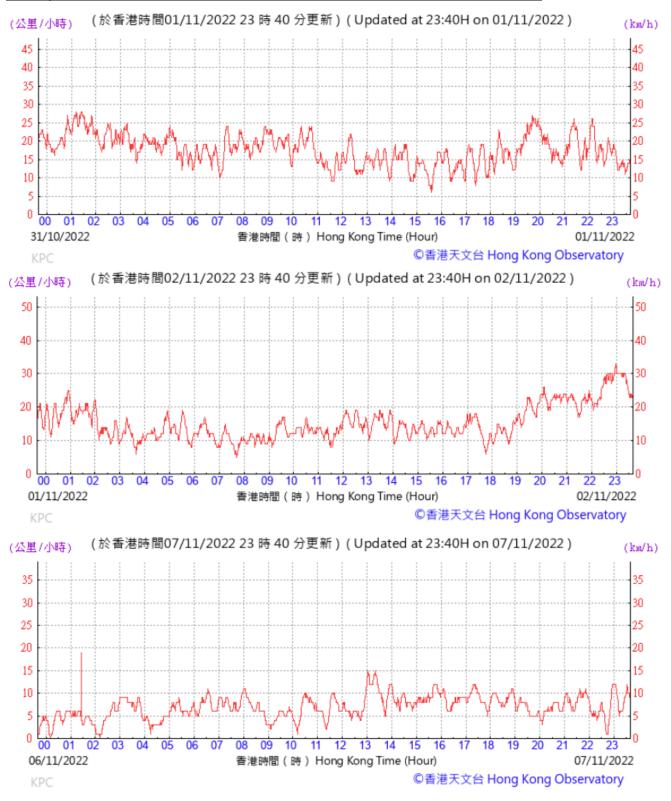


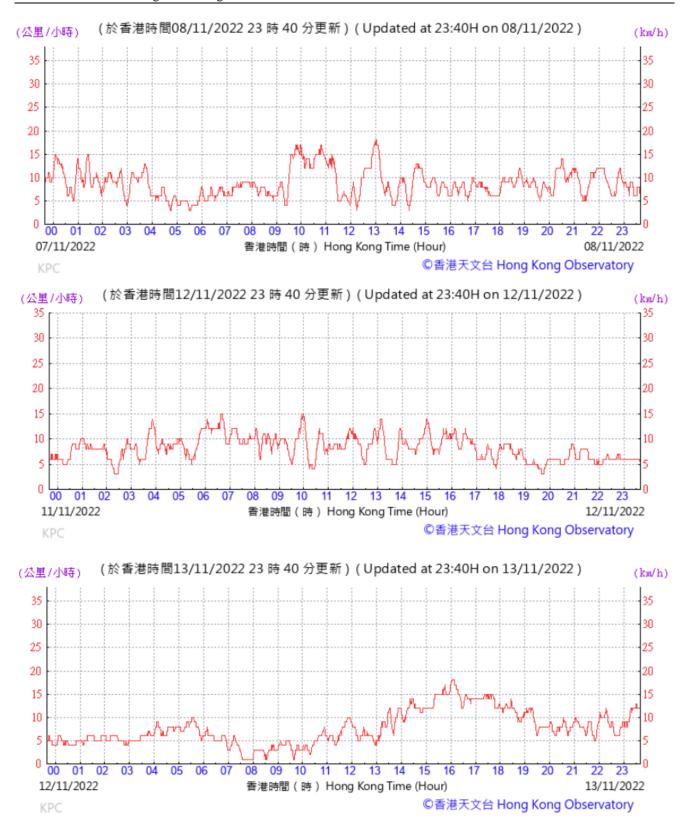

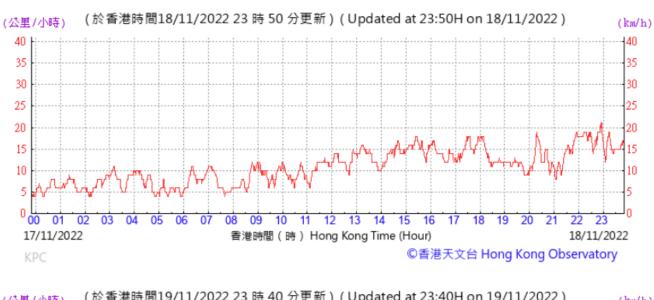





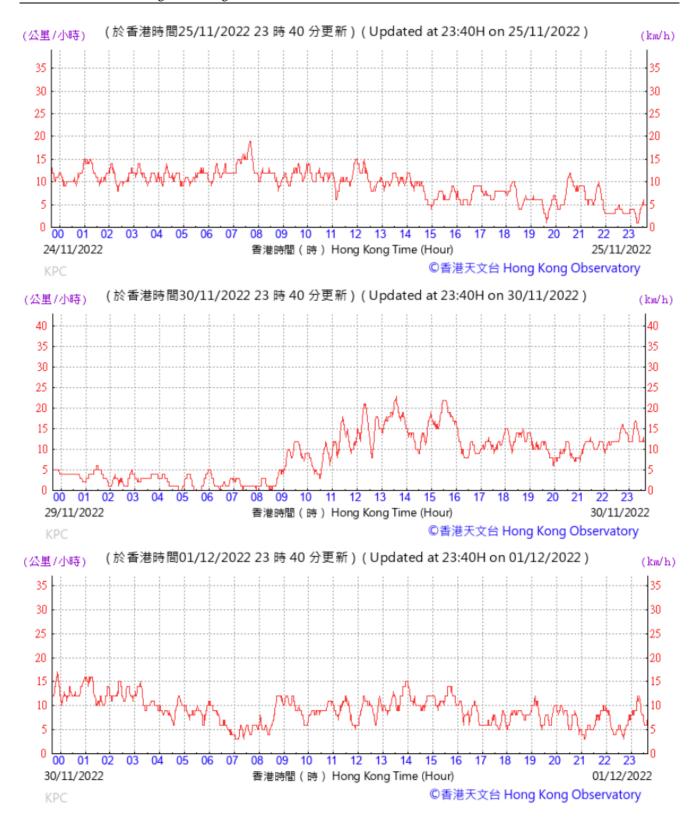

Contract No. HY/2014/08
Environmental Monitoring & Auditing

Appendix M
Monitoring Data (Noise)

Location: Yau Ma Tei Catholic Primary School (Hoi Wang Road) (W-N1A)

Monitoring date: 1, 7, 12, 18, 24 and 30 November 2022

 $\begin{array}{ll} \text{Parameter:} & L_{\text{eq}},\,L_{10},\,L_{90} \\ \text{Other Factors} & \text{Nearby traffic} \end{array}$

Date	Weather	Start Time	-	End Time	$L_{\rm eq}$	L_{10}	L ₉₀	Wind speed (m/s)
01/11/2022	Fine	10:10	-	10:40	61.3	63.4	57.7	3.4
07/11/2022	Fine	9:37	-	10:07	62.5	63.8	58.0	1.8
12/11/2022	Fine	9:40	-	10:10	61.3	63.3	56.9	2.7
18/11/2022	Fine	9:02	-	9:32	61.2	63.4	57.4	3.6
24/11/2022	Cloudy	12:47	-	13:17	60.4	62.5	57.6	3.4
30/11/2022	Fine	12:51	-	13:21	60.0	62.3	56.9	4.1

Remark: 1. Examination was carried out at Yau Ma Tei Catholic Primary School between 14 to 22 November 2022. The limit level of W-N1A would be 65 dB(A) on 18 November 2022. The limit level of W-N1A would be 70 dB(A) on 1, 7, 12, 24 and 30 November 2022.

Location: Hydan Place (W-N18)

Monitoring date: 1, 7, 12, 18, 24 and 30 November 2022

 $\begin{array}{ll} Parameter: & L_{eq}, L_{10}, \ L_{90} \\ Other \ Factors & Nearby \ traffic \end{array}$

Date	Weather	Start Time	-	End Time	$L_{\rm eq}$	L_{10}	L_{90}	Wind speed (m/s)
01/11/2022	Fine	13:31	-	14:01	70.7	73.2	67.0	4.2
07/11/2022	Fine	13:58	-	14:28	70.6	73.1	67.4	3.4
12/11/2022	Fine	14:41	-	15:11	71.7	74.3	67.8	2.8
18/11/2022	Fine	10:43	-	11:13	70.5	73.5	66.3	2.7
24/11/2022	Cloudy	10:03	-	10:33	70.2	73.3	66.6	3.6
30/11/2022	Fine	9:57	-	10:27	72.0	73.3	68.1	2.4

Location: Prosperous Garden Block 1 (W-N25A)

Monitoring date: 1, 7, 12, 18, 24 and 30 November 2022

 $\begin{array}{ll} \text{Parameter:} & L_{\text{eq.}}L_{10,}\;L_{90} \\ \text{Other Factors} & \text{Nearby traffic} \end{array}$

Date	Weather	Start Time	-	End Time	$L_{\rm eq}$	L_{10}	L ₉₀	Wind speed (m/s)
01/11/2022	Fine	12:47	-	13:17	70.8	74.1	66.9	3.4
07/11/2022	Fine	13:03	-	13:33	70.3	73.7	67.1	2.8
12/11/2022	Fine	13:57	-	14:27	70.4	74.0	67.7	3.4
18/11/2022	Fine	9:59	-	10:29	69.2	73.7	67.2	3.6
24/11/2022	Cloudy	9:16	-	9:46	68.3	71.6	65.8	4.5
30/11/2022	Fine	10:39	-	11:09	71.1	73.1	68.2	2.3

Location: The Coronation Tower 1 (W-P11)

Monitoring date: 1, 7, 12, 18, 24 and 30 November 2022

 $\begin{array}{ll} Parameter: & L_{eq}, L_{10}, L_{90} \\ Other \ Factors & Nearby \ traffic \end{array}$

Date	Weather	Start Time	-	End Time	$L_{\rm eq}$	L_{10}	L ₉₀	Wind speed (m/s)
01/11/2022	Fine	11:03	-	11:33	67.1	68.9	64.7	4.1
07/11/2022	Fine	10:29	-	10:59	67.1	69.0	65.1	2.7
12/11/2022	Fine	15:38	-	16:08	65.9	68.2	63.3	2.9
18/11/2022	Fine	11:38	-	12:08	66.6	68.4	63.2	3.5
24/11/2022	Cloudy	11:15	-	11:45	66.0	67.9	64.3	4.2
30/11/2022	Fine	11:34	-	12:04	65.1	67.0	63.5	3.9

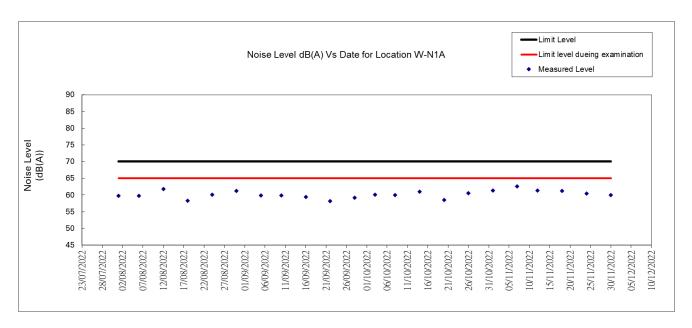


Figure 1: Graphical Illustration of Measured Noise Levels at W-N1A

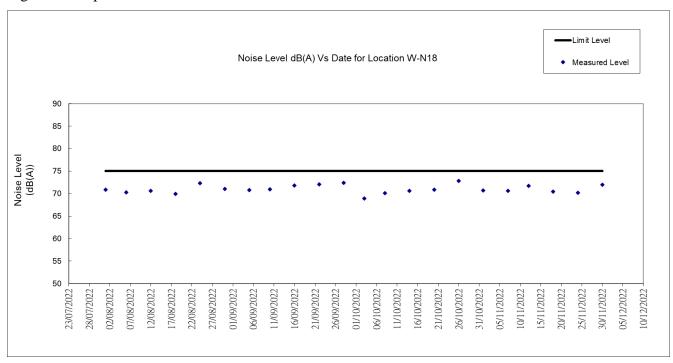


Figure 2: Graphical Illustration of Measured Noise Levels at W-N18

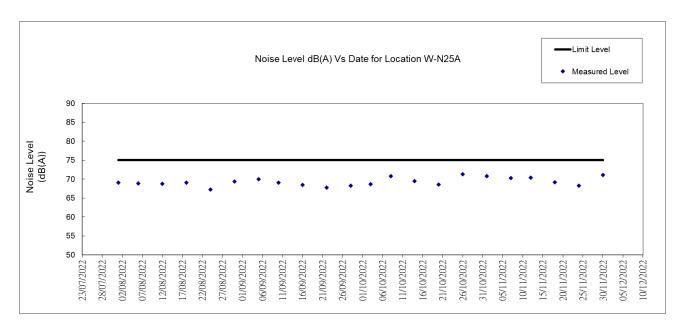


Figure 3: Graphical Illustration of Measured Noise Levels at W-N25A

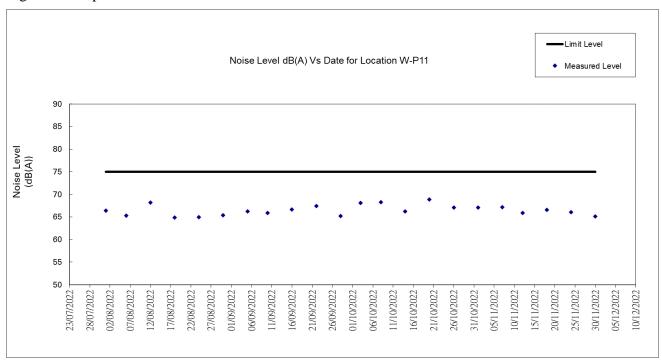


Figure 4: Graphical Illustration of Measured Noise Levels at W-P11

Contract No. HY/2014/08	
Environmental Monitoring & Auditing	2

Appendix N
Waste Flow Table

Monthly Summary Waste Flow Table

Highways Department Name of Department:

Contract No. / Works Order No.: HY/2014/08

Monthly Summary Waste Flow Table for November 2022

[to be submitted not later than the 15th day of each month following reporting month] (All quantities shall be rounded off to 1 decimal place.)

		Actual Quantities of <u>Inert</u> Construction Waste Generated Monthly				
Month	(a)=(b)+(c)+(d)+(e)+ (f)+ (g)+ (h)+ (i)+ (j)+ (k) Total Quantity Generated	(b) Hard Rock and Large Broken	(c) Reused in the Contract	(d) Reused in other Projects	(e) Disposed of as Public Fill	(f) Imported Fill
	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)	(in 'tonnes)
Jan-22	7033.91	116.10	232.40	4412.20	2227.40	0.00
Feb-22	1808.80	157.80	435.30	590.60	557.10	0.00
Mar-22	4333.20	39.20	99.00	1114.20	3043.30	0.00
Apr-22	15700.00	214.50	995.80	9387.70	4998.00	0.00
May-22	11192.90	55.20	42.00	2335.40	8719.30	0.00
Jun-22	8364.90	378.70	0.00	0.00	7942.70	0.00
Sub-total	48433.71	961.50	1804.50	17840.10	27487.80	0.00
Jul-22	5848.70	444.30	0.00	0.00	5359.40	0.00
Aug-22	13080.81	1222.40	0.00	0.00	11768.20	0.00
Sep-22	14957.00	298.60	0.00	0.00	14596.30	0.00
Oct-22	14239.70	531.10	0.00	0.00	13636.50	0.00
Nov-22	12532.70	16.70	0.00	104.00	12362.10	0.00
Dec-22						
Total	109092.62	3474.60	1804.50	17944.10	85210.30	0.00
2018	51057.90	0.00	0.00	0.00	47715.60	2877.40
2019	112830.10	541.00	1523.80	13525.00	93132.90	3155.60
2020	193021.92	58778.00	1205.60	19108.60	112556.80	0.00
2021	104679.02	6461.30	1393.70	1144.70	92950.20	1542.90
Accumulated Total	570681.56	69254.90	5927.60	51722.40	431565.80	7575.90

	Actual Quantities of <u>Non-inert</u> Construction Waste Generated Monthly								
Month	(; Me	g) tals	(h) Paper/ cardboard packaging		(i Plas) tics	(j) Chemical Waste		(k) Others, e.g. General Refuse disposed at Landfill
	(in '0	00kg)	(in '00	00kg)	(in '00	00kg)	(in '0	00kg)	(in 'tonnes)
	generated	recycled	generated	recycled	generated	recycled	generated	recycled	generated
Jan-22	0.00	0.00	0.00	0.00	0.01	0.00	0.00	0.00	45.80
Feb-22	43.90	0.00	0.60	0.00	0.00	0.00	0.00	0.00	23.50
Mar-22	0.00	0.00	0.20	0.00	0.00	0.00	0.80	0.00	36.50
Apr-22	64.70	0.00	0.60	0.00	0.00	0.00	0.00	0.00	38.70
May-22	0.00	0.00	0.20	0.00	0.00	0.00	0.40	0.00	40.40
Jun-22	0.00	0.00	0.50	0.00	0.00	0.00	0.00	0.00	43.00
Sub-total	108.60	0.00	2.10	0.00	0.01	0.00	1.20	0.00	227.90
Jul-22	0.00	0.00	0.30	0.00	0.00	0.00	0.00	0.00	44.70
Aug-22	0.00	0.00	0.70	0.00	0.01	0.00	0.00	0.00	89.50
Sep-22	0.00	0.00	0.20	0.00	0.00	0.00	0.00	0.00	61.90
Oct-22	0.00	0.00	0.00	0.10	0.00	0.00	0.00	0.00	72.00
Nov-22	0.00	0.00	0.00	0.10	0.00	0.00	0.00	0.00	49.80
Dec-22									
Total	108.60	0.00	3.30	0.20	0.02	0.00	1.20	0.00	545.80
2018	28.40	0.00	0.00	0.00	0.00	0.00	2.00	0.00	434.50
2019	0.00	9.10	3.40	6.80	0.00	0.00	5.20	0.00	927.30
2020	69.20	0.00	3.30	0.00	0.02	0.00	25.30	0.00	1275.10
2021	30.20	0.00	4.80	0.00	0.02	0.00	25.50	0.00	1125.70
Accumulated Total	236.40	9.10	14.80	7.00	0.06	0.00	59.20	0.00	4308.40



Appendix O
Statistics on Complaint, Notifications of
Summons and Successful Prosecutions

Statistical Summary of Exceedances

	Air Quality							
Reporting Period	Action Level	Limit Level						
1 November 2022-	0	0						
30 November 2022	U	U						
	Noise							
Reporting Period	Action Level	Limit Level						
1 November 2022-	1	0						
30 November 2022	4	U						

Statistical Summary of Environmental Complaints

D 41 D 1 1		Environmental Complaint Statistics				
Reporting Period	Frequency	Cumulative	Complaint Nature			
1 November 2022-			-			
30 November	4	46	Construction noise			
2022						

Statistical Summary of Environmental Non-compliance


Domontino Dominal	En	vironmental Non-compliance S	Statistics
Reporting Period	Frequency	Cumulative	Details
1 November 2022-			
30 November	0	1	N/A
2022			

Statistical Summary of Environmental Summons


Statistical Summing of Silvinoimiental Summons								
Donouting Donied	Environmental Summons Statistics							
Reporting Period	Frequency	Cumulative	Details					
1 November 2022-								
30 November	0	1	N/A					
2022								

Statistical Summary of Environmental Prosecution

	Statistical Sallina	y of Environmental Flosecati	OII .
Donauting Davied		Environmental Prosecution Sta	atistics
Reporting Period	Frequency	Cumulative	Details
1 November 2022-			
30 November	0	0	N/A
2022			




		Imp	pact Monitoring Schedule for Y	MTE		
			Dec-22			
Sun	Mon	Tue	Wed			Sat
			<u> </u>	1	2	3
4	5	6	7	8	9	10
		Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A				
11	12	13	14	15	16	17
	Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A					Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A
18	19	20	21	22	23	24
					Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A	
25	26	27	28	29	30	31
				Impact Air monitoring for W-A6 &W-A1 Noise monitoring for W-N1A, W-P11,W-N18 & W-N25A		



Interim Report on Environmental Complaint

Project	Central Kowloon Route, Yau Ma Tei East Section
Complaint Code	EC045-CKRYMTE20221111_001
Complaint description	Two complaints were received on 11 November 2022, which complained about the construction noise from the site area near Gascoigne Road Flyover during daytime recently, and junction of Shanghai Street and Gansu Street at 7:00 am for nearly half year.
Parameter	Construction Noise
Investigation finding	The 1 st complaint was received on 11 November 2022 and was concerned about the construction noise from near Gascoigne Road Flyover during daytime. The complainant did not specify the concerning date and therefore we assume the investigation period would be between 12 October to 11 November 2022.
	Regarding construction noise generated from near Gascoigne Road Flyover, as noted by the contractor, noise enclosure installation works were carried out at Zone 3 Noise Enclosure only in the investigation period during daytime. The complaint was mentioned about the "strong noise (suspected to be material drop-off into metal container" generated from Zone 3 Noise Enclosure. However, unpleasant noise was not observed during weekly environmental inspection site walks. Weekly noise impact monitoring was conducted, and the results were below limit level. No exceedance of limit level in noise impact monitoring was observed in the investigation period.
	Proper noise mitigation measures have been well-implemented by the contractor at the Zone 3 Noise Enclosure in the investigation period with reference to the suggestion listed in the approved EM&A manual and Section 3.2 of CNMMP (Rev.16.1) which includes:
	 a) Temporary noise barriers had been erected nearby the noisy machines or plants to screen noise effectively from Noise Sensitive Receivers (NSRs). b) Sequentially operating noisy equipment to alleviate noise impacts from construction activities to the NSRs. c) All machines and plants were planned to be located as far as the surrounding NSRs to avoid disturbance.
	d) Quieter equipment was selected to minimize noise nuisance.e) All machines and plants would be shut down when they are not in use to minimize noise emission.
	The 2 nd complaint was received on 11 November 2022 and was concerned about the construction noise from Zone D3 (near junction of Shanghai Street and Gansu Street) at 7:00 am for nearly half year. The investigation period of the complaint would be between 11 May 2022 to 11 November 2022.
	Regarding construction noise generated from Zone D3, the complaint was mentioned about the loud noise generated from dumping excavated materials to vehicles by excavator. As noted by the contractor, excavation works were conducted within permitted hours under the stipulated NCO requirement, whereas only excavated soil was disposed to dump trucks by excavators. Strong noise was unlikely to come from soil disposal. According to weekly inspection site walks during the investigation period, no environmental deficiency regarding to construction noise was observed at Zone D3. The results of weekly noise impact monitoring in the investigation period were below the limit level. No exceedance in noise impact monitoring was observed in the investigation period. In addition, the excavation works at Zone D3 were started from September 2022 as confirmed by the contractor. The concerned construction noise for nearly half-year period was unlikely to come from Zone D3. Therefore, the 2 nd complaint was concluded non-project related.
	Considering the fulfillment of stipulated requirements by the Contractor for EM&A manual and CNMMP, it is concluded that there was no non-compliance to the EM&A requirement of the Project regarding noise impact from construction site.

Actions taken / to be taken	mitigation measur In view of public of Provide single alleviate in Provide tr	es in order to minim concerns, the follow te supervision to en loise impacts aining and notice to	A Manual and CNMMP strictly to implement nize nuisance to the public. Ving additional remedial measures are taken: nsure the noise barriers had been proper erected to of frontline workers to remind them when loading or conduct carefully to avoid excessive noise
Remarks		eation at Zone 3 Noi	
(Shown in next page)	2. Works loc	ation at Zone D3	
Prepared by ET (Acuity Sustainability Consulting Limited)	Janice Lee	p	
Reviewed by ETL (Acuity Sustainability Consulting Limited)	Kevin Li	X.	
Verified by IEC (ERM-Hong Kong, Limited)	Mandy To	Mandy 2.	
Date	17 Novem	ber 2022	

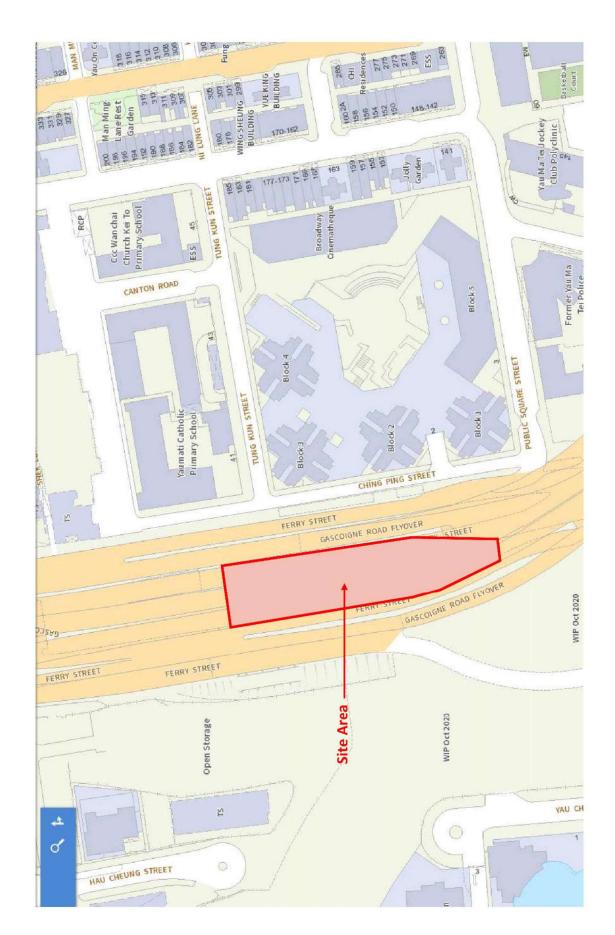

Remark 1: Works location at Zone 3 Noise Enclosure



Remark 2: Works location at Zone D3

Interim Report on Environmental Complaint

Project	Central Kowloon Route, Yau Ma Tei East Section
Complaint Code	EC045-CKRYMTE20221114_001
Complaint description	The complainant complained about the construction noise from the site located at the
	junction of Shanghai Street and Gansu Street.
Parameter	Construction Noise
Investigation finding	The complaint was received on 14 November 2022 and was concerned about the construction noise from the site located at the junction of Shanghai Street and Gansu Street. The concerning site area was not contracted in this project. For this project, the nearest site which involved excavation works is Zone D3. The complainant did not specify the concerning date and therefore we assume the investigation period would be on 1 month basis, which is between 15 October to 14 November 2022.
	The complaint mentioned the loud noise generated from concerning site area, especially from operating the excavator. As noted by the contractor, excavation works were conducted at Zone D3 within permitted hours under the stipulated NCO requirement, whereas only excavated soil was loaded by excavators. It was believed that strong noise was unlikely to come from loading and unloading activities of excavated soil. According to weekly inspection site walks during the investigation period, no environmental deficiency regarding construction noise was observed at Zone D3. The results of weekly noise impact monitoring in the investigation period were below the limit level. No exceedance of limit level in noise impact monitoring was observed in the investigation period.
	Proper noise mitigation measures have been well-implemented by the contractor at Zone D3 in the investigation period with reference to the suggestion listed in the approved EM&A manual and Section 3.2 of CNMMP (Rev.16.1) which includes:
	 a) Temporary noise barriers had been erected nearby the noisy machines or plants to screen noise effectively from Noise Sensitive Receivers (NSRs). b) Sequentially operating noisy equipment to alleviate noise impacts from construction activities to the NSRs. c) All machines and plants were planned to be located as far as the surrounding NSRs to avoid disturbance.
	The concerning site area was not belongs to this project and the concerning construction noise was believed that not come from Zone D3. Thus, the complaint was concluded as non-project related.
	Considering the fulfillment of stipulated requirements by the Contractor for EM&A manual and CNMMP, it is concluded that there was no non-compliance of the Project regarding noise impact from construction site.
Actions taken / to be taken	The Contractor had followed EM&A Manual and CNMMP strictly to implement mitigation measures in order to minimize nuisance to the public. In view of public concerns, the following additional remedial measures are taken:
	Provide site supervision to ensure the noise barriers had been proper erected to alleviate noise impacts Provide training and action to frontline analysis to grantline and the grantline
	 Provide training and notice to frontline workers to remind them when loading or unloading materials shall be conduct carefully to avoid excessive noise
Remarks	1. Works location at Zone D3
(Shown in next page)	

Prepared by ET (Acuity Sustainability Consulting Limited)	Janice Lee	Ja
Reviewed by ETL (Acuity Sustainability Consulting Limited)	Kevin Li	K
Verified by IEC (ERM-Hong Kong, Limited)	Mandy To	Mandy2.
Date	18 Novem	ber 2022



Remark 1: Works location at Zone D3


Interim Report on Environmental Complaint

Project	Central Kowloon Route, Yau Ma Tei East Section
Complaint Code	EC047-CKRYMTE20221116_001
Complaint description	The complainant complained about the equipment generating noise from the site near Kansu Street during the past Saturday night, Sunday, and high frequency noise during daytime and seeking prompt reply.
Parameter	Construction Noise
Investigation finding	The complaint was received on 17 November 2022 and was concerned about the construction noise from the site near Kansu Street on 12 November 2022 (Sat) night and 13 November 2022 (Sun) at daytime.
	According to the video provided by the complainant, continuous sound levels were recorded. As noted by the contractor, the concerned area was suspected to be Zone D3 where no construction work was conducted during the concerned period, while water pumps, submersible (electric) were deployed on the basement level for collecting groundwater. A valid Construction Noise Permit (CNP) (Permit No:GW-RE1210-22) was granted from EPD on 10 November 2022 with coverage of the construction site at Kansu Street between Canton Road and Reclamation Street near Yau Ma Tel Jockey Club Polyclinic, which indicated as Working Zone A and Working Zone B. The concerned area, Zone D3, was included in Working Zone B of CNP. The water pump, submersible (electric) was identified in PME Group C of CNP, which maximum five water pumps were allowed to operate simultaneously during 0700-2300 on general holidays and 1900 – 2300 on any day not being a general holiday in Working Zone A and Working Zone B. No water pump, submersible (electric) was operated in Working Zone A during the concerned period. As recorded by the contractor, two water pumps, submersible (electric), were operated at Zone D3 during 1900-2200 on 12 November 2022 and 0800-2200 on 13 November 2022. No violation and non-compliance of CNP was observed or recorded. The contractor had followed the requirements as stipulated in CNP.
	According to weekly inspection site walks in November 2022, no environmental deficiency regarding construction noise was observed at Zone D3.
	Proper noise mitigation measures have been well-implemented by the contractor at Zone D3 in the investigation period with reference to the suggestion listed in the approved EM&A manual and Section 3.2 of CNMMP (Rev.16.1) which includes:
	 a) Temporary noise barriers had been erected nearby the noisy machines or plants to screen noise effectively from Noise Sensitive Receivers (NSRs). b) Sequentially operating noisy equipment to alleviate noise impacts from construction activities to the NSRs. c) All machines and plants were planned to be located as far as the surrounding NSRs to avoid disturbance.
	Considering the fulfillment of stipulated requirements by the Contractor for EM&A manual, CNMMP and CNP (Permit No:GW-RE1210-22), it is concluded that there was no non-compliance of the Project regarding noise impact from construction site.
Actions taken / to be taken	The Contractor had followed EM&A Manual, CNMMP and granted CNP strictly to implement mitigation measures in order to minimize nuisance to the public.
	 In view of public concerns, the following additional remedial measures are taken: Provide site supervision to ensure the noise barriers had been proper erected to alleviate noise impacts; Provide training and notice to frontline workers to remind them to switch off PME when not in use to avoid excessive noise; Review the working hour and method to reduce noise nuisance to NSRs during event and night-time; Carry out site inspection at day end to ensure all PME were switched off.

Remarks (Shown in next page)		cation at Zone D3 rier at Zone D3
Prepared by ET (Acuity Sustainability Consulting Limited)	Janice Lee	p
Reviewed by ETL (Acuity Sustainability Consulting Limited)	Kevin Li	K
Verified by IEC (ERM-Hong Kong, Limited)	Mandy To	Mandy 2.
Date	23 Novem	nber 2022



Remark 1: Works location at Zone D3

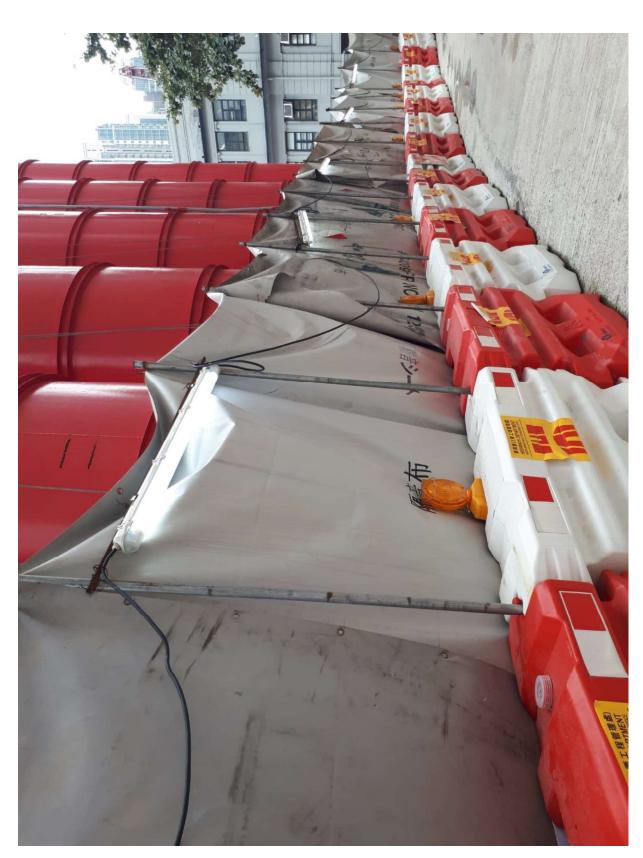

Remark 2: Noise barrier at Zone D3
