



Water Supplies Department
New Works Branch
Construction Division
11 Tai Yip Lane
Kowloon Bay
Kowloon
Hong Kong

Your reference:

Our reference: HKWSD201/50/106967

Date: 24 December 2020

Attention: Mr Y M Chan

BY POST

Quotation No.: WQ/17/A071
Independent Environmental Checker for Water Supplies Department
– Proposed Desalination Plant in TKO Area 137 for Contract No. 13/WSD/16
Verification of Monthly EM&A Report No.28

We refer to email of 22 December 2020 attaching Monthly EM&A Report No.28 for the captioned project prepared by the ET.

We have no comment and hereby verify the Monthly EM&A Report No.28 in accordance with Clause 3.5 of the Environmental Permit no. EP-503/2015/A.

Should you have any queries regarding the above, please do not hesitate to contact the undersigned or our Ms Reasonlie Cheung on 2618 2831.

Yours faithfully
ANewR CONSULTING LIMITED

James Choi
Independent Environmental Checker

CPSJ/LYMA/CYYR/lsmr



ACUITY
SUSTAINABILITY
CONSULTING LIMITED



Website: www.acuityhk.com



Unit C, 11/F, Ford Glory Plaza,
Nos. 37-39 Wing Hong Street,
Cheung Sha Wan, Kowloon.



Tel. : (852) 2698 6833
Fax.: (852) 2698 9383



水務署

Water Supplies Department



Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

Monthly EM&A Report No. 28
(Period from 1 to 30 November 2020)

December 2020

(Rev. 0)

	Prepared by:	Certified by:
Name	Karen Cheung	Jacky Leung
Position	Environmental Team	Environmental Team Leader
Signature		
Date:	21/12/2020	21/12/2020

Revision History

0	1 st Submission	21 Dec 2020
Rev.	DESCRIPTION OF MODIFICATION	DATE

CONTENT

Executive Summary	
1. Basic Project Information	8
2. Noise Monitoring.....	12
3. Waste management	17
4. Landfill gas monitoring	18
5. Summary of Monitoring Exceedance, Complaints, Notification of Summons and Prosecutions	34
6. EM&A Site Inspection	35
7. Future Key Issues	37
8. Conclusion and Recommendations.....	39

Appendix A	Construction Programme
Appendix B	Overview of Mainlaying in Tseung Kwan O
Appendix C	Summary of Implementation Status of Environmental Mitigation
Appendix D	Impact Monitoring Schedule of the Reporting Month
Appendix E	Noise Monitoring Equipment Calibration Certificate
Appendix F	Event/Action Plan for Noise Exceedance
Appendix G	Noise Monitoring Data
Appendix H	Waste Flow Table
Appendix I	Landfill Gas Monitoring Equipment Calibration Certificate
Appendix J	Landfill Gas Monitoring Data
Appendix K	Complaint Log and Regulatory Compliance Proforma
Appendix L	Site Inspection Proforma
Appendix M	Proactive Environmental Protection Proforma
Appendix N	Impact Monitoring Schedule of Next Reporting Month
Appendix O	Academic Calendar(s)
Appendix P	Interim Report for the Complaint

EXECUTIVE SUMMARY

Introduction

- A1. Penta-Ocean - Concentric Joint Venture (POCJV) is contracted to carry out the Mainlaying in Tseung Kwan O under Contract No. 13/WSD/16 (hereinafter known as “the Project”).
- A2. In accordance with the Environmental Monitoring and Audit (EM&A) Manual for the Project, EM&A works should be carried out by Environmental Team (ET), Acuity Sustainability Consulting Limited (ASCL), during the construction phase of the Project.
- A3. This is the 28th Monthly EM&A Report, prepared by ASCL, for the Project summarizing the monitoring results and audit findings of the EM&A programme at and around Tseung Kwan O (TKO) during the reporting period from 1 November 2020 to 30 November 2020.
- A4. The EM&A programme for this contract has covered environmental monitoring on construction noise level at selected NSRs and Contractor’s environmental performance auditing in the aspects of construction dust, construction noise, water quality, waste management, Landscape and Visual and Ecology.

Summary of Main Works Undertaken & Key Mitigation Measures Implemented

- A5. Key works carried out in this reporting period for the Project included the followings:

Location	Location	Works Conducted in the reporting month
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> Hydrostatic pressure testing for completed MS1200 pipeline section. Backfilling and reinstatement work.
	TKO 137 Pit A	<ul style="list-style-type: none"> Grouting works for ELS of trenchless receiving pit was completed. Pipe trench excavation and ELS works were in-progress.
	TKO 137 Pit B	<ul style="list-style-type: none"> Pipe trench excavation and ELS works were in-progress
	TKO 137 Pit C	<ul style="list-style-type: none"> Pipe piling and ELS works were in-progress
Portion J of the Project Site	Wan Po Rd – Workfront 1	<ul style="list-style-type: none"> Pipe trench excavation and pipe laying were in-progress.
	Wan Po Rd – Workfront 2	<ul style="list-style-type: none"> Pipe trench excavation and pipe laying were in-progress.
	Wan Po Rd – Workfront 3	<ul style="list-style-type: none"> Construction of remaining works for IT chamber was in-progress.
	Wan Po Rd – Pit A	<ul style="list-style-type: none"> Pit excavation and ELS works.
	Wan Po Rd – Pit B	<ul style="list-style-type: none"> Additional pipe pile was completed. Hole drilling and installing grout tube for re-grouting were in progress.

Location	Location	Works Conducted in the reporting month
	Wan Po Rd – Pit C	<ul style="list-style-type: none"> Construction of receiving pit was completed.
	Landfill Stage 1 – Area A	<ul style="list-style-type: none"> Trench excavation and pipe laying were conducted.
	Landfill Stage 1 – Area B	<ul style="list-style-type: none"> Trench excavation and pipe laying were as conducted.
	Cycle Track – Workfront 1	<ul style="list-style-type: none"> Trench excavation and pipe laying were in-progress.
	Cycle Track – Workfront 2	<ul style="list-style-type: none"> Trench excavation and pipe laying were in-progress.
	Velodrome – Pit L	<ul style="list-style-type: none"> Sheet piling for pit ELS was completed.
	Velodrome – Pit M	<ul style="list-style-type: none"> Pipe jacking works were conducted.
	Velodrome – Pit N	<ul style="list-style-type: none"> Receiving pit was completed.
	Velodrome – Pit O	NA
	Velodrome – Pit P	<ul style="list-style-type: none"> Grouting works was in-progress.
	Mau Wu Tsai	<ul style="list-style-type: none"> Trial pit and trench excavation were conducted.

A6. The major environmental impacts brought by the above construction works include:

- Construction dust and noise generation of saw cutting of concrete surface, mainlaying of pipes, hole-drilling, grouting, excavation works and installation works.
- Waste generation from the construction activities

A7. The key environmental mitigation measures implemented for the Project in this reporting period associated with the above construction works include:

- Dust suppression by regular wetting and water spraying during saw cutting of concrete surface, mainlaying of pipes, hole-drilling, grouting, excavation works and installation works
- Reduction of noise from equipment and machinery on-site
- Sorting and storage of general refuse and construction waste

Summary of Exceedance & Investigation & Follow-up

A8. Noise monitoring was conducted in the reporting month for NSR4 Creative Secondary School on 6, 12, 18 and 27 November 2020 as construction works were conducted within 300m to the noise sensitive receiver. No project-related exceedance of the Action Level was recorded during the reporting period.

Complaint Handling and Prosecution

- A9. One project-related environmental complaint was received during the reporting period.
- A10. Neither notifications of summons nor prosecution was received for the Project.

Reporting Change

- A11. There were no changes reported that may affect the on-going EM&A programme.

Summary of Upcoming Key Issues and Key Mitigation Measures

- A12. Key works in December 2020 (the next reporting month) for the Project will include the followings:

Location	Location	Forecast Works for November 2020
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> Preparation works and hydrostatic pressure testing for completed MS1200 pipeline section will be conducted.
	TKO 137 Pit A	<ul style="list-style-type: none"> Pit ELS and excavation works will be continued.
	TKO 137 Pit B	<ul style="list-style-type: none"> Pit ELS and excavation works will be continued.
	TKO 137 Pit C	<ul style="list-style-type: none"> Pit pipe piling for ELS works will be continued.
Portion J of the Project Site	Wan Po Rd – Workfront 1	<ul style="list-style-type: none"> Trench excavation and pipe laying will be conducted.
	Wan Po Rd – Workfront 2	<ul style="list-style-type: none"> Trench excavation and pipe laying works will be conducted. Road reinstatement and TTA shifting to next stage will be conducted.
	Wan Po Rd – Workfront 3	<ul style="list-style-type: none"> Construction for IT chamber will be continued. Trench excavation and mainlaying works will be conducted.
	Wan Po Rd – Pit A	<ul style="list-style-type: none"> Excavation and ELS works will be conducted.
	Wan Po Rd – Pit B	N/A
	Wan Po Rd – Pit C	N/A
	Landfill Stage 1 – Area A	<ul style="list-style-type: none"> Trench excavation and pipe laying works will be conducted.
	Landfill Stage 1 – Area B	<ul style="list-style-type: none"> Trench excavation and pipe laying works will be conducted.
	Cycle Track – Workfront 1	<ul style="list-style-type: none"> Trench excavation and pipe laying works will be conducted.

Location	Location	Forecast Works for November 2020
	Cycle Track – Workfront 2	<ul style="list-style-type: none"> Trench excavation and pipe laying works will be conducted.
	Velodrome – Pit L	<ul style="list-style-type: none"> Pit excavation will be conducted.
	Velodrome – Pit M	<ul style="list-style-type: none"> Pipe jacking works will be continued.
	Velodrome – Pit N	N/A
	Velodrome – Pit O	<ul style="list-style-type: none"> Establishment for pipe jacking works will be completed.
	Velodrome – Pit P	<ul style="list-style-type: none"> Grouting works will be completed. Pit excavation and ELS works will be resumed
	Mau Wu Tsai	<ul style="list-style-type: none"> Trench excavation and pipe mainlaying works will be conducted.

A13. The major environmental impacts brought by the above construction works will include:

- Construction dust and noise generation of saw cutting of concrete surface, mainlaying of pipes, pipe piling, grouting, excavation works and installation works.
- Waste generation from construction activities

A14. The key environmental mitigation measures for the Project in the coming reporting period associated with the above construction works will include:

- Dust suppression by regular wetting and water spraying for saw cutting of concrete surface, mainlaying of pipes, pipe piling, grouting, excavation works and installation works.
- Reduction of noise from equipment and machinery on-site
- Sorting and storage of general refuse and construction waste

1. BASIC PROJECT INFORMATION

1.1 Background

1.1.1 The proposed Desalination Plant at Tseung Kwan O (DPTKO) will produce potable water with an initial capacity of 135 million liters per day (MLD), expandable to an ultimate capacity of 270 MLD in the future to provide a secure and alternative fresh water resource complying with the World Health Organization (WHO) standards. The plant will adopt the Seawater Reverse Osmosis (SWRO) technology, which dominates the market due to its reliability and progressive reduction in cost as the technology advances.

1.1.2 Pursuant to the Environmental Impact Assessment Ordinance (EIAO), the Director of Environmental Protection granted the Variation of Environmental Permit (No. EP-503/2015/A) to Water Supplies Department (WSD) for the Project on 26 January 2018.

1.1.3 The scope of the Contract may be considered in brief, to consist of the laying of about 10km long 1200mm diameter fresh water mains and the associated works along the alignment of the Project as shown with the overall view in **Appendix B**.

1.2 The Reporting Scope

1.2.1 This is the 28th Monthly EM&A Report for the Project which summarizes the key findings of the EM&A programme during the reporting period from 1 November 2020 to 30 November 2020.

1.3 Project Organization

1.3.1 The Project Organization structure for Construction Phase is presented in **Figure 1.1**.

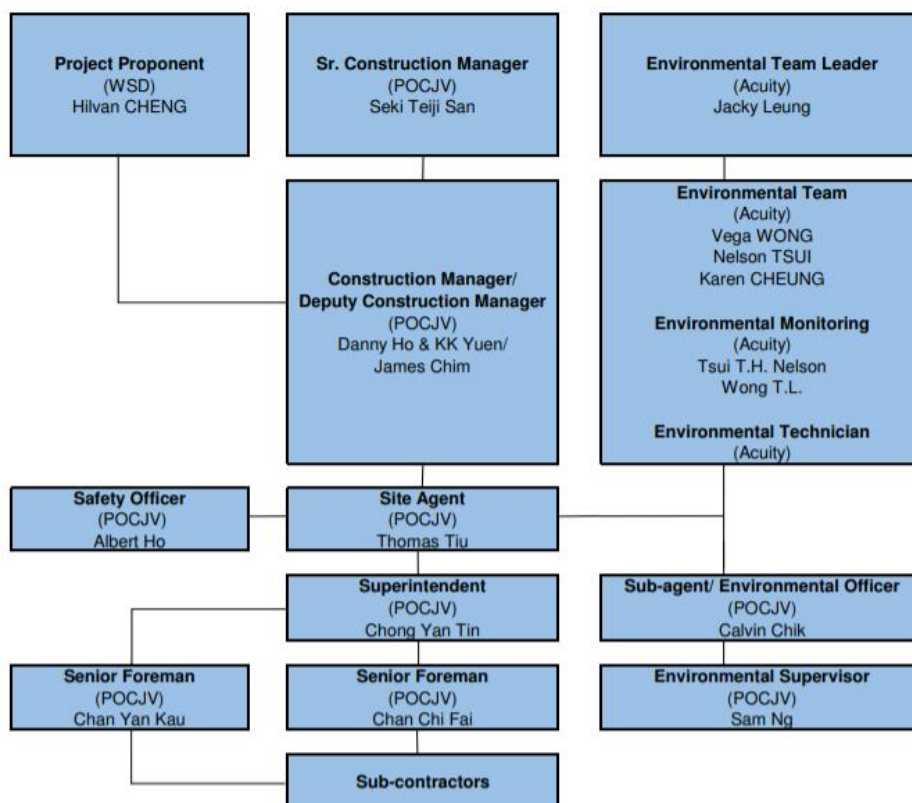


Figure 1.1 Project Organization Chart

1.3.2 Contact details of the key personnel are presented in **Table 1.1** below:

Party	Position	Name	Telephone no.
Penta-Ocean Concentric Joint Venture	Environmental Officer	Calvin Chik	9863 5630
Acuity Sustainability Consulting Limited	Environmental Team Leader	Jacky Leung	2698 6833
ANewR Consulting Limited	Independent Environmental Checker	James Choi	2618 2831

1.4 Summary of Construction Works

1.4.1 Details of the major construction works undertaken in this reporting period are shown in **Table 1.2** and the construction works locations are

shown in **Appendix B**. The construction programme is presented in **Appendix A**.

Table 1.2 Summary of the Construction Works Undertaken during the Reporting Month

Progress of work activities (Completed)		
Location	Location	Works Conducted in the reporting month
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> Backfilling and reinstatement works were completed.
	TKO 137 Pit A	<ul style="list-style-type: none"> Pipe pile for ELS for trenchless receiving pit and relevant grouting works were completed.
Portion J of the Project Site	Wan Po Rd – Pit B	<ul style="list-style-type: none"> Additional pipe pile was completed.
	Velodrome – Pit C	<ul style="list-style-type: none"> Receiving pit construction was completed.
	Velodrome – Pit L	<ul style="list-style-type: none"> Pit sheet piling was completed.
	Velodrome – Pit N	<ul style="list-style-type: none"> Receiving pit was completed.

Progress of work activities (In Progress)		
Location	Location	Works Conducted in the reporting month
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> Preparation works and hydrostatic pressure testing for completed MS1200 pipeline section.
	TKO 137 Pit A	<ul style="list-style-type: none"> Pit excavation and ELS works.
	TKO 137 Pit B	<ul style="list-style-type: none"> Pit excavation and ELS works.
	TKO 137 Pit C	<ul style="list-style-type: none"> Pit pipe piling and ELS works.
Portion J of the Project Site	Wan Po Rd – Workfront 1	<ul style="list-style-type: none"> Pipe trench excavation and pipe laying were in-progress.
	Wan Po Rd – Workfront 2	<ul style="list-style-type: none"> Pipe trench excavation and pipe laying were in-progress.
	Wan Po Rd – Workfront 3	<ul style="list-style-type: none"> Construction of remaining works for IT chamber was in progress.
	Wan Po Rd – Pit A	<ul style="list-style-type: none"> Pit excavation and ELS works.
	Wan Po Rd – Pit B	<ul style="list-style-type: none"> Hole drilling and installing grout tube for re-grouting were in progress.
	Landfill Stage 1 – Area A	<ul style="list-style-type: none"> Trench excavation and pipe laying were conducted.
	Landfill Stage 1 – Area B	<ul style="list-style-type: none"> Trench excavation and pipe laying were conducted.
	Cycle Track – Workfront 1	<ul style="list-style-type: none"> Trench excavation and pipe laying were in-progress.
	Cycle Track – Workfront 2	<ul style="list-style-type: none"> Trench excavation and pipe laying were in-progress.
	Velodrome – Pit M	<ul style="list-style-type: none"> Pipe jacking works were in-progress.

Progress of work activities (In Progress)		
Location	Location	Works Conducted in the reporting month
	Velodrome – Pit O	<ul style="list-style-type: none"> Establishment for pipe jacking works was in-progress.
	Velodrome – Pit P	<ul style="list-style-type: none"> Grouting works were in progress.
	Mau Wu Tsai	<ul style="list-style-type: none"> Trial pit and trench excavation.

1.5 Summary of Environmental Status

1.5.1 A summary of the valid permits, licences, and or notifications on environmental protection for this Project is presented in **Table 1.3**.

Table 1.3 Summary of the Status of Valid Environmental Licence, Notification, Permit and Documentations

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Variation of Environmental Permit	EP no.: EP-503/2015/A	Throughout the Contract	-
Notification of Construction Works under the Air Pollution Control (Construction Dust) Regulation (Form NA)	Ref no.: 423775	Throughout the Contract	-
Chemical Waste Producer Registration	WPN: 5213-839-P3287-01	Throughout the Contract	-
Billing Account for Disposal of Construction Waste	A/C no.: 7029491	Throughout the Contract	-
Water Discharge Licence	WT00032336-2018	Until 31 Dec 2023	-
Construction Noise Permit	GW-RE0846-20	Until 31 Mar 2021	-
Construction Noise Permit (Hong Kong Velodrome)	GW-RE0364-20	Until 17 Nov 2020	-
Construction Noise Permit (Hong Kong Velodrome)	GW-RE0961-20	Until May 2021	-
Construction Noise Permit (Landfill Stage 1 near Jockey Club HKFA Football Training Centre)	GW-RE0927-20	Until 24 Jan 2021	-

1.5.2 The status for all environmental aspects is presented **Table 1.4**.

Table 1.4 Summary of Status for Key Environmental Aspects under the EM&A Manual

Parameters	Status
Noise	
Baseline Monitoring	The baseline noise monitoring result has been reported in Baseline Monitoring Report and submitted to EPD under VEP Condition 3.4.
Impact Monitoring	On-going
Waste Management	
Mitigation Measures in Waste Monitoring Plan	On-going
Landfill Gas	
Impact Monitoring	On-going
Environmental Audit	
Site Inspection	On-going

1.5.3 Other than the EM&A works by ET, regular environmental management meetings were conducted in order to enhance environmental awareness and closely monitor the environmental performance of the contractors.

1.5.4 The EM&A programme has been implemented in accordance with the recommendations presented in the approved EIA Report and the EM&A Manual. A summary of implementation status of the environmental mitigation measures for the construction phase of the Project during the reporting period is provided in **Appendix C**.

2. NOISE MONITORING

2.1 Monitoring Requirements

2.1.1 To ensure no adverse noise impact, noise monitoring is recommended to be carried out within 300m radius from the nearby noise sensitive receivers (NSRs), during construction phase. The NSRs selected as monitoring station are (i) NSR4 – Creative Secondary School, (ii) NSR24 – PLK Laws Foundation College, and (iii) NSR31 – School of Continuing and Professional Studies – CUHK respectively.

2.1.2 In accordance with the EM&A Manual, baseline noise level at the noise monitoring stations were established as presented in the Baseline Monitoring Report. Impact noise monitoring will be conducted once per week in the form of 30-minute measurements Leq, L10 and L90 levels recorded at each monitoring station between 0700 and 1900 on normal weekdays.

2.1.3 Referring to EM&A manual Section 4.1.2, the impact noise monitoring should be carried out at all the designated monitoring stations when there are project-related construction activities undertaken within a radius of 300m from the monitoring stations.

2.1.4 Impact monitoring for noise impact was conducted in the reporting month for NSR4 – Creative Secondary School on 6, 12, 18, and 27 November 2020 as construction works were conducted within 300m to the noise sensitive receiver. Detailed monitoring results can be found in **Appendix G**.

2.2 Noise Monitoring Parameters, Time, Frequency

2.2.1 Impact noise monitoring was conducted weekly in the reporting period between 0700-1900 on normal weekdays. No construction works were carried out during 1900-0700 in all days or any time on Sundays or general holidays during the reporting period.

2.2.2 Construction noise level measured in terms of the A-weighted equivalent continuous sound pressure level (LAeq). Leq_{30min} was used as the monitoring parameter for the time period between 0700 and 1900 on normal weekdays. **Table 2.1** summarizes the monitoring parameters, frequency and duration of the impact noise monitoring. The monitoring schedule is provided in **Appendix D**.

Table 2.1 Noise Monitoring Parameters, Time, Frequency and Duration

Time	Frequency	Duration	Parameters
Daytime: 0700-1900	Once per week	Continuously in Leq _{5min} /Leq _{30min} (average of 6 consecutive Leq _{5min})	Leq, L ₁₀ & L ₉₀

2.3 Noise Monitoring Locations

2.3.1 The monitoring locations should normally be made at a point 1m from the exterior of the NSRs building façade and be at a position 1.2m above the ground. A correction of +3dB(A) should be made to the free-field measurements.

2.3.2 According to the environmental findings detailed in the EIA report and Baseline Monitoring Report, the designated locations for the construction noise monitoring are listed in **Table 2.2** below.

Table 2.2 Noise Monitoring Location

NSR ID	Noise Sensitive Receivers	Monitoring Location	Position
NSR 4	Creative Secondary School	Roof Floor	1 m from facade
NSR 24	PLK Laws Foundation College	Pedestrian Road on Ground Floor	Free-field
NSR 31	School of Continuing and Professional Studies - CUHK	Roof Floor	1 m from facade

2.3.3 Three noise monitoring locations for impact monitoring at the nearby sensitive receivers are shown in **Figure 2.1-2.3**.

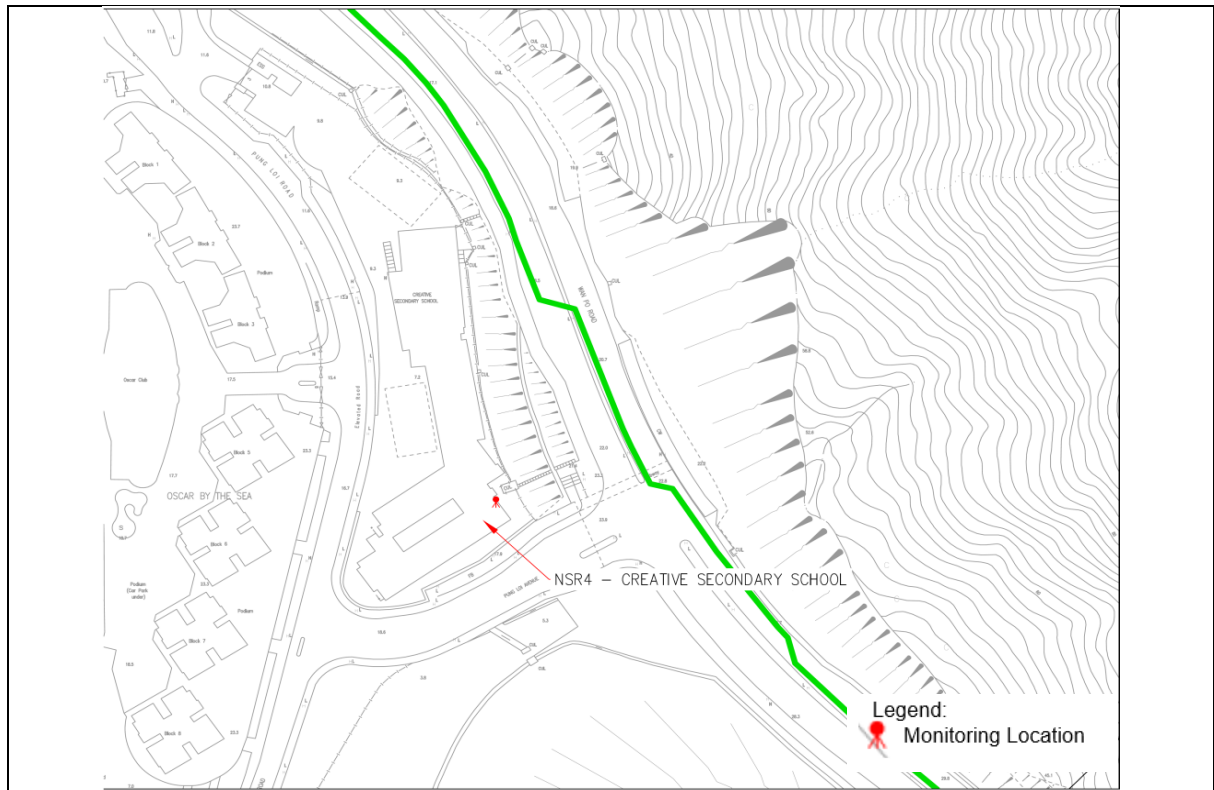


Figure 2.1 NSR4 Creative Secondary School


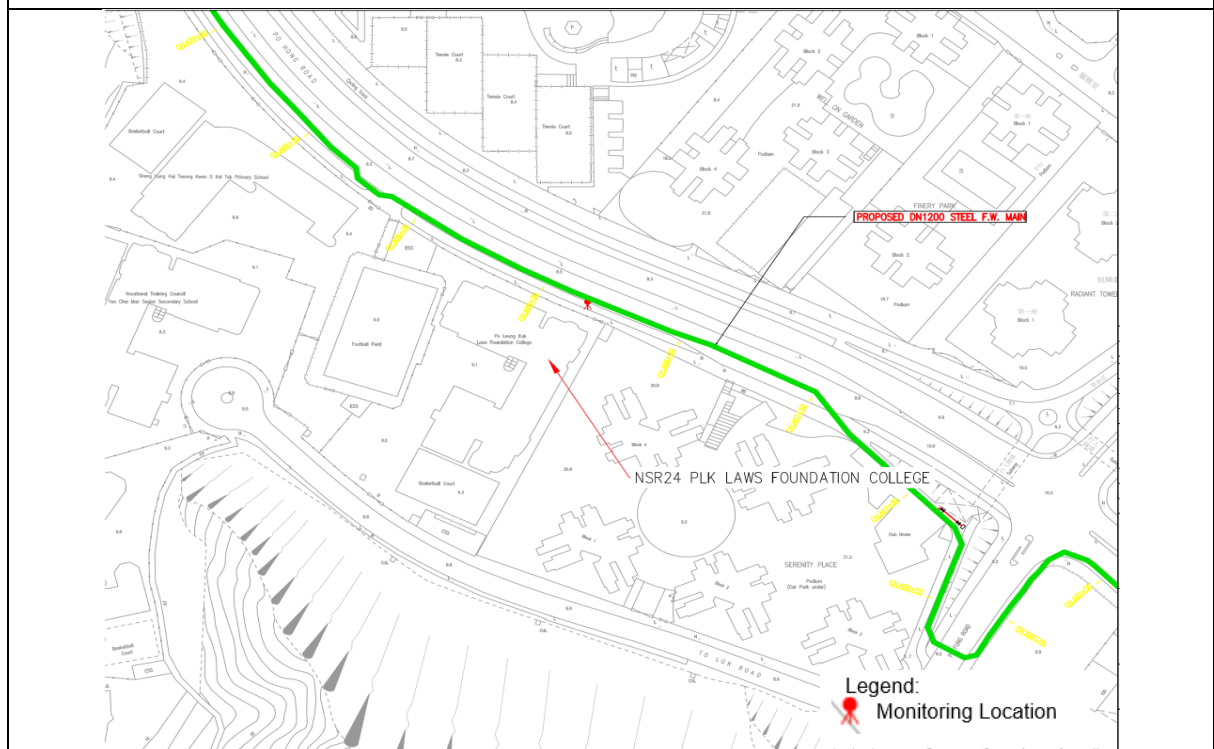


Figure 2.2 NSR24 PLK Laws Foundation College

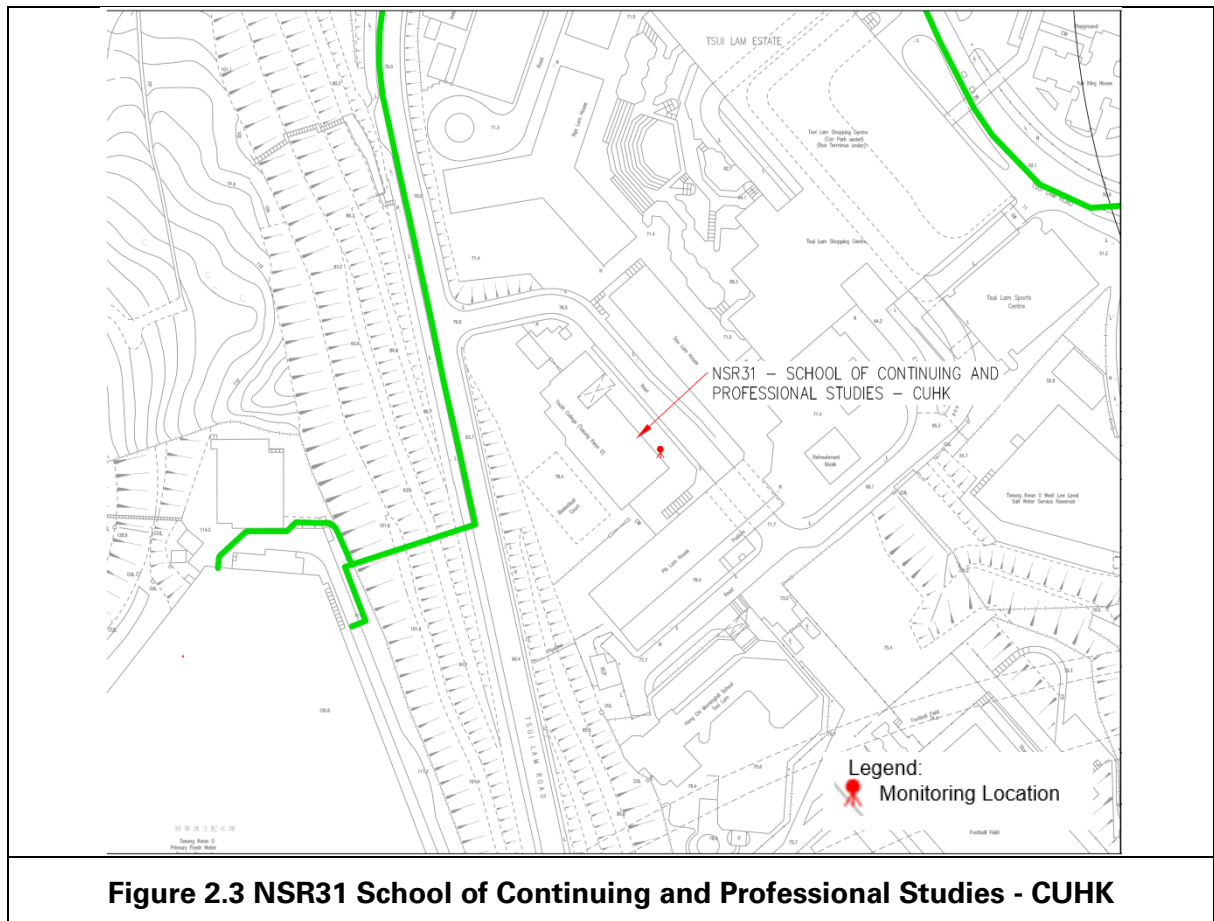

2.4 Impact Monitoring Methodology

- 2.4.1 Integrated sound level meter shall be used for the noise monitoring. The meter shall be in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level before and after the noise measurements agree to within 1.0 dB(A). Calibration certificates of the instruments used are presented in **Appendix E**.
- 2.4.2 Noise measurements shall not be made in the presence of fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

2.4.3 Table 2.3 Impact Noise Monitoring Equipment

Equipment	Brand and Model	Detection Limit
Sound Level Meter	Nti XL2	30-130 dB(A)
Sound Level Meter Calibrator	Pulsar 105	Nil
Pocket Wind Meter Anemometer	Kestrel 1000 Wind Meter	Nil

2.5 Action and Limit Levels

2.5.1 The Action/Limit Levels are in line with the criteria of Practice Note for Professional Persons (ProPECC PN 2/93) "Noise from Construction Activities – Non-statutory Controls" and Technical Memorandum on Environmental Impact Assessment Process issued by HKSAR Environmental Protection Department ["EPD"] under the Environmental Impact Assessment Ordinance, Cap 499, S.16 are presented in **Table 2.4**.

Table 2.4 Action and Limit Levels for Noise

Time Period	Action	Limit (dB(A))
0700-1900 on normal weekdays	When one documented complaint is received from any one of the noise sensitive receivers	<ul style="list-style-type: none"> • 70 dB(A) for school and • 65 dB(A) during examination period
Notes: (a) Limits specified in the GW-TM and IND-TM for construction and operation noise, respectively.		

2.5.2 If exceedances were found during noise monitoring, the actions in accordance with the Event and Action Plan shall be carried out according to **Appendix F**.

2.6 Monitoring Results and Observations

2.6.1 Referring to EM&A manual Section 4.1.2, impact monitoring for noise impact was conducted in the reporting month for NSR4 – Creative Secondary School on 6, 12, 18 and 27 november 2020.

2.6.2 Detailed monitoring results are presented in **Appendix G**.

3. WASTE MANAGEMENT

3.1 The waste generated from this Project includes inert construction and demolition (C&D) materials, and non-inert C&D materials. Non-inert C&D materials are made up of general refuse, vegetative wastes and recyclable wastes such as plastics and paper/cardboard packaging waste. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in **Table 3.1**. Details of cumulative waste management data are presented as a waste flow table in **Appendix H**.

Table 3.1 Quantities of waste generated from the Project

Reporting period	Quantity					
	Inert C&D Materials (in '000m3)	Chemical Waste (in '000kg)	Non-inert C&D Materials			
			Others, e.g. General Refuse disposed at Landfill (in '000m3)	Recycled materials		
				Paper/card board (in '000kg)	Plastics (in '000kg)	Metals (in '000kg)
November-20	2.180	0.000	0.003	0.056	0.000	0.000

4. LANDFILL GAS MONITORING

4.1 Monitoring Requirement

4.1.1 In accordance with Section 11 of the EM&A Manual, monitoring of landfill gas is required for construction works within the 250m Consultation Zone. Part of the desalination plant and the indicative area of natural slope mitigation works fall within the SENT Landfill Extension Consultation Zone; and part of the 1,200 mm diameter fresh water mains along Wan Po Road falls within the SENT Landfill and SENT Landfill Extension Consultation Zones, TKO Stage II/III Restored Landfill and TKO Stage I Restored Landfill Consultation Zones.

4.2 Monitoring Location

4.2.1 Monitoring of oxygen, methane, carbon dioxide and barometric pressure was performed for excavations at 1m depth or more within the consultation Zone. In this reporting period, 706 times of monitoring was recorded.

4.2.2 During construction of works within the consultation zones, excavations of 1m depth or more was monitored:

- At the ground surface before excavation commences;
- Immediately before any worker enters the excavation;
- At the beginning of each working day for the entire period the excavation remains open; and
- Periodically through the working day whilst workers are in the excavation.

4.2.3 For excavations between 300mm and 1m deep, measurements should be carried out:

- Directly after the excavation has been completed; and
- Periodically whilst the excavation remains open.

4.2.4 The area required to be monitored for landfill gas in the reporting period are shown in **Figure 4.1** to **Figure 4.15**.

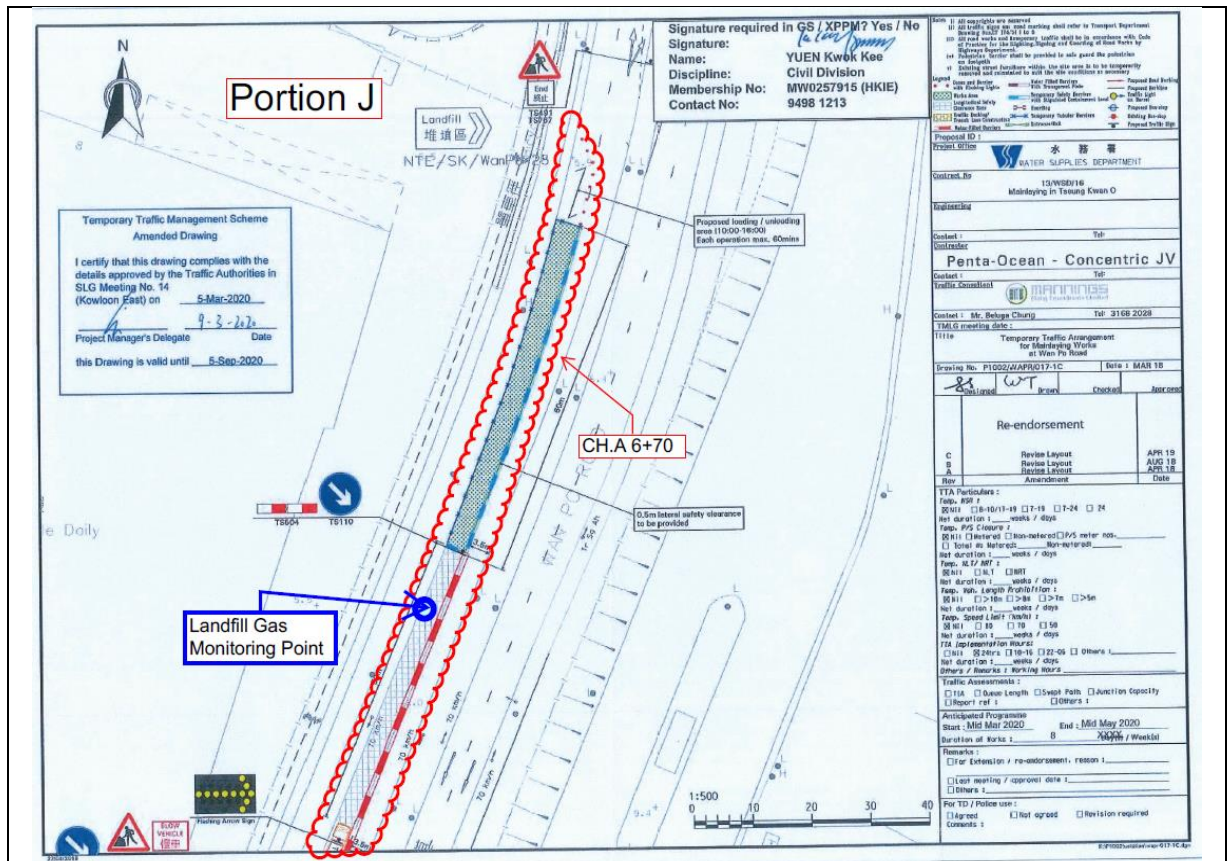


Figure 4.1 Monitoring Location - CH.A 6+70

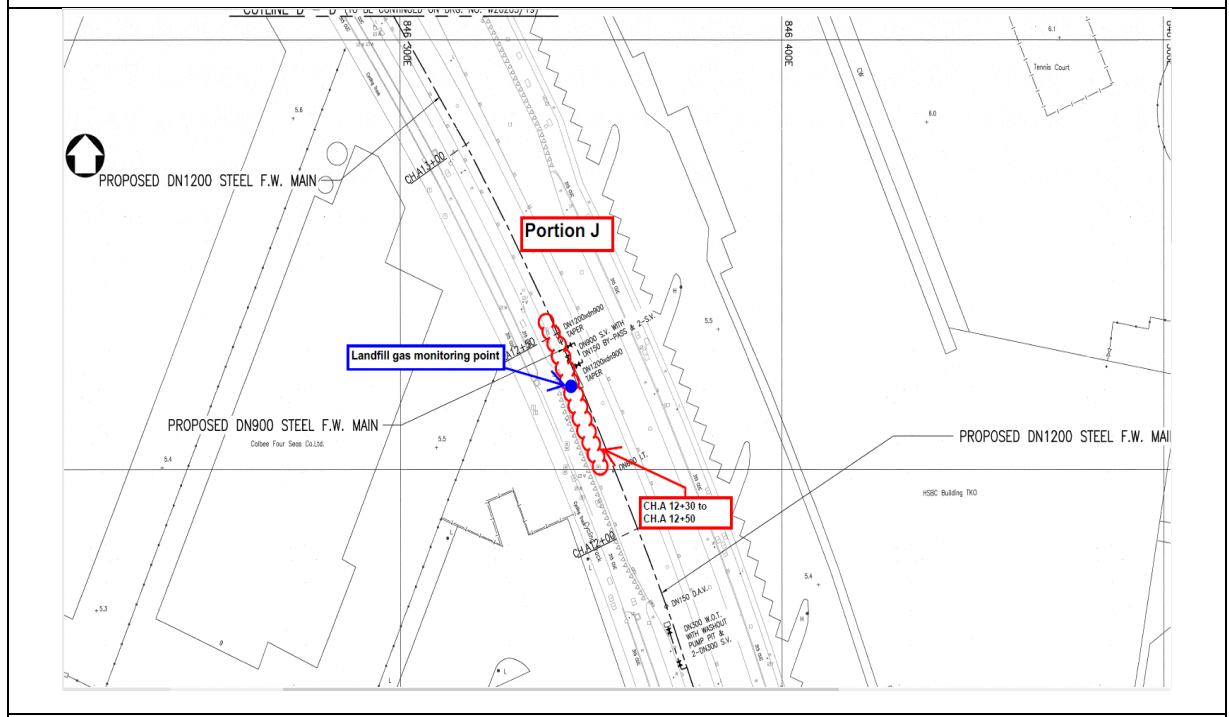


Figure 4.2 Monitoring Location - CH.A 12+30 ~ 12+50

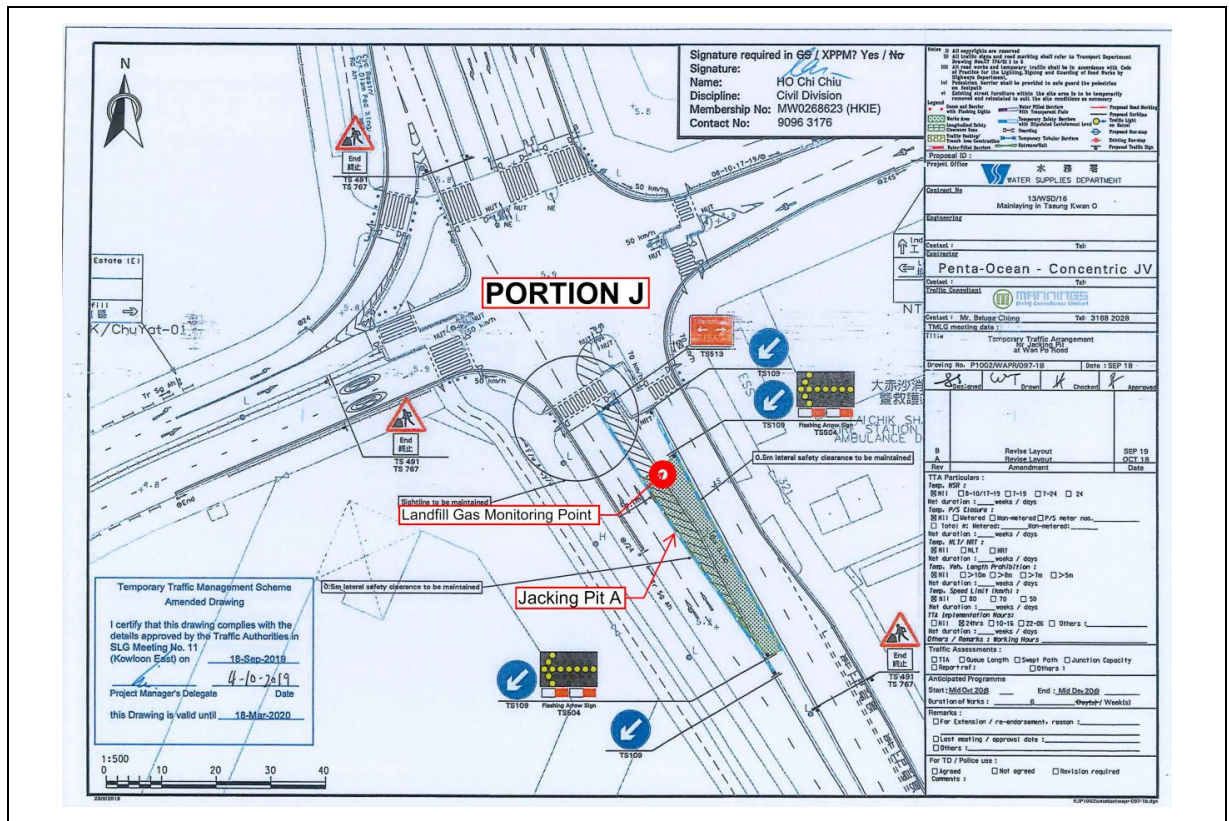


Figure 4.3 Monitoring Location – CH.A 13+50 ~ 14+00 (Pit A)

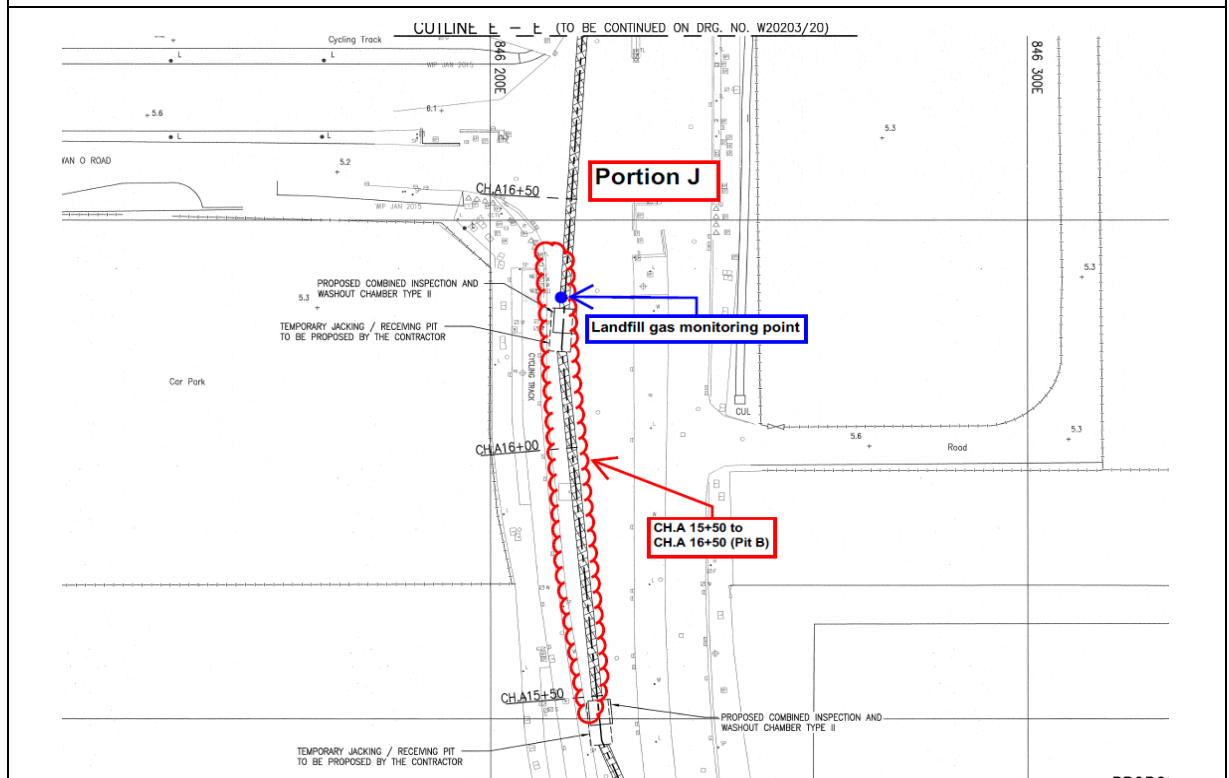


Figure 4.4 Monitoring Location – CH.A 15+50 ~ 16+50 (Jacking Pit B)

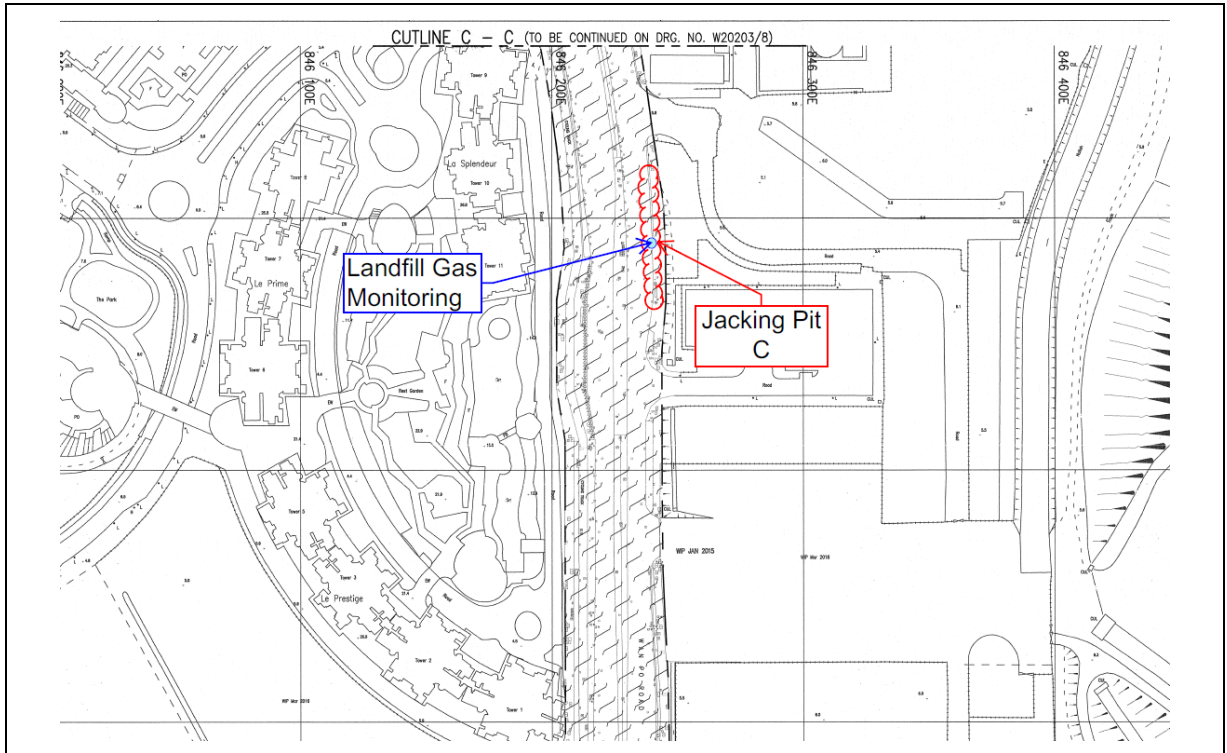


Figure 4.5 Monitoring Location – CH.A 19+15 ~19+50 (Pit C)

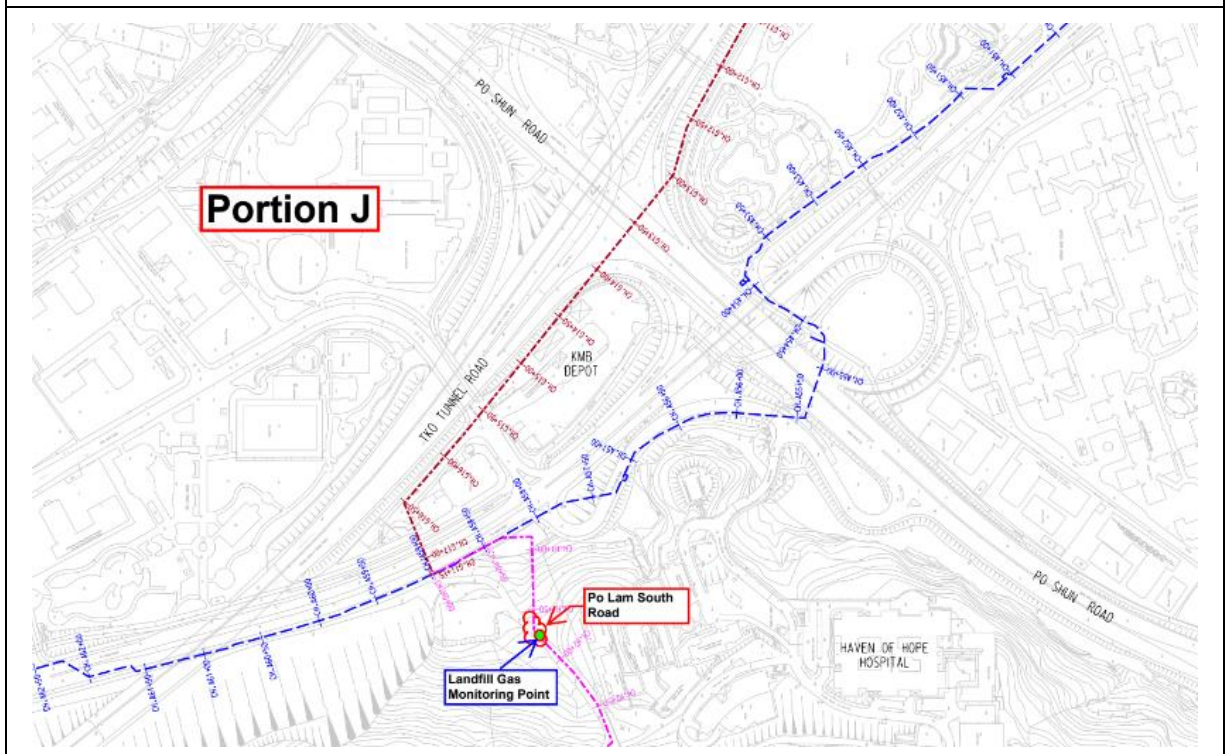


Figure 4.6a Monitoring Location – Mau Wu Tsai 1

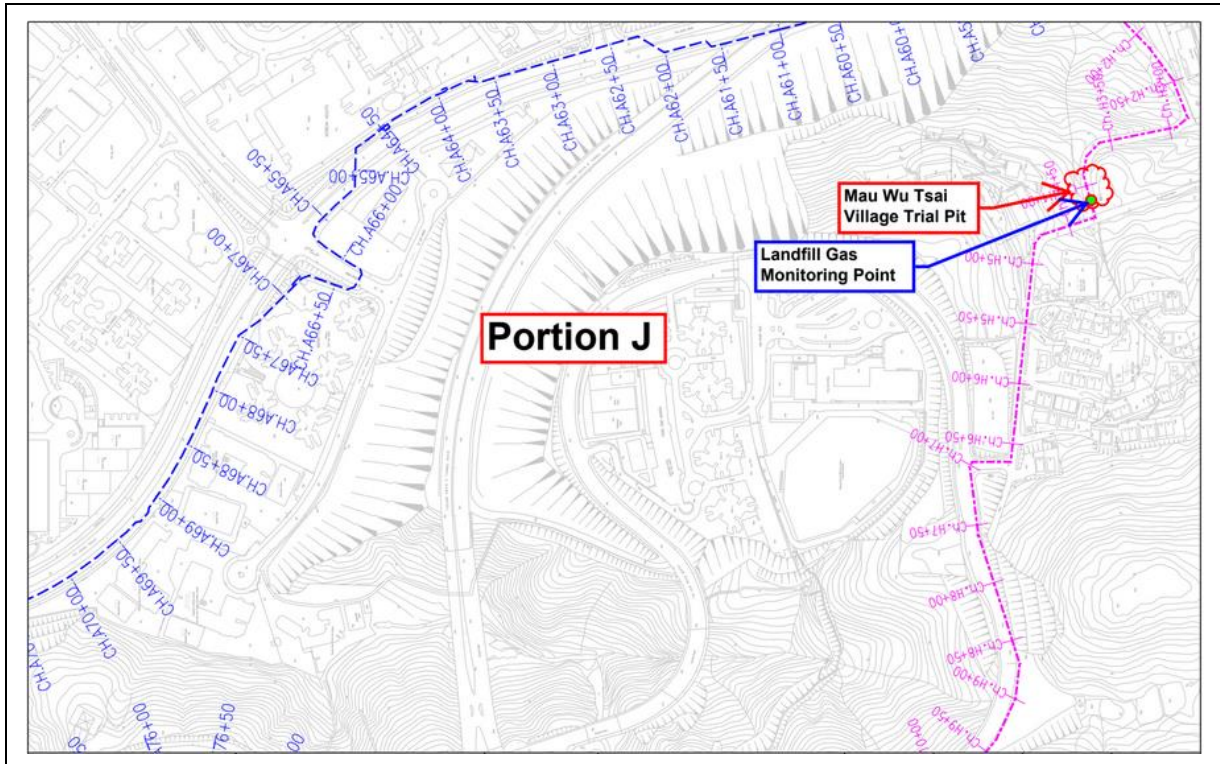


Figure 4.6b Monitoring Location – Mau Wu Tsai 2

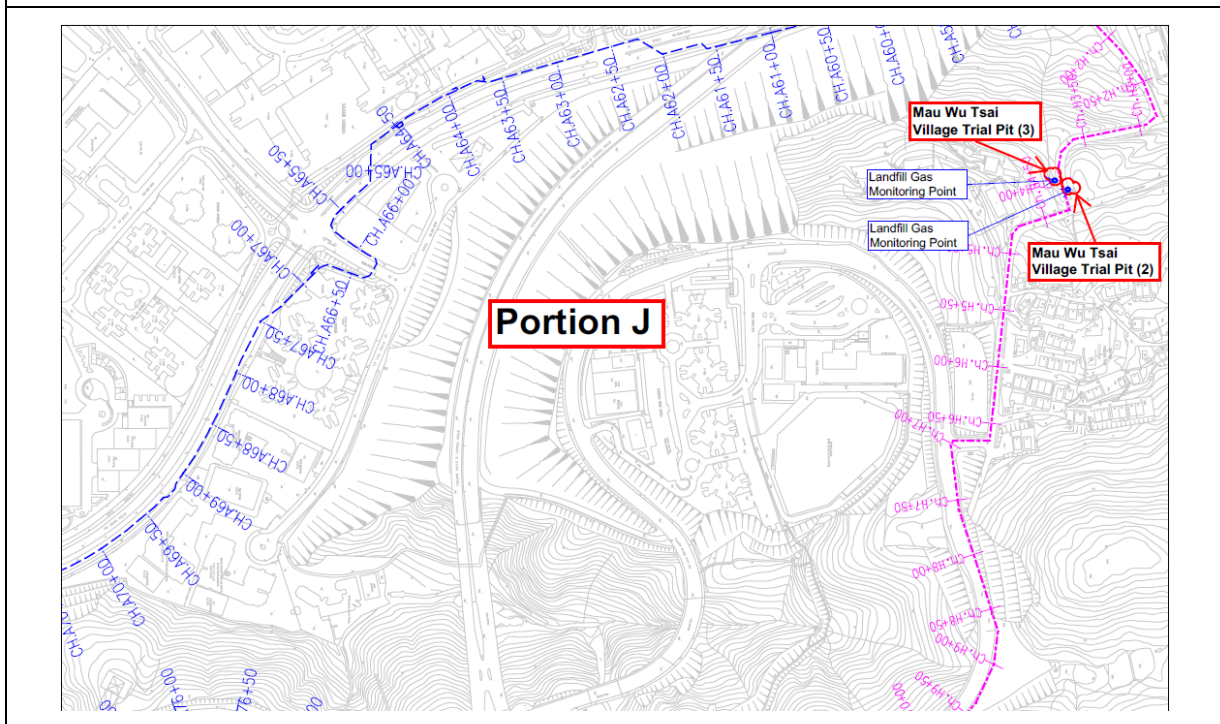


Figure 4.6c Monitoring Location – Mau Wu Tsai 3

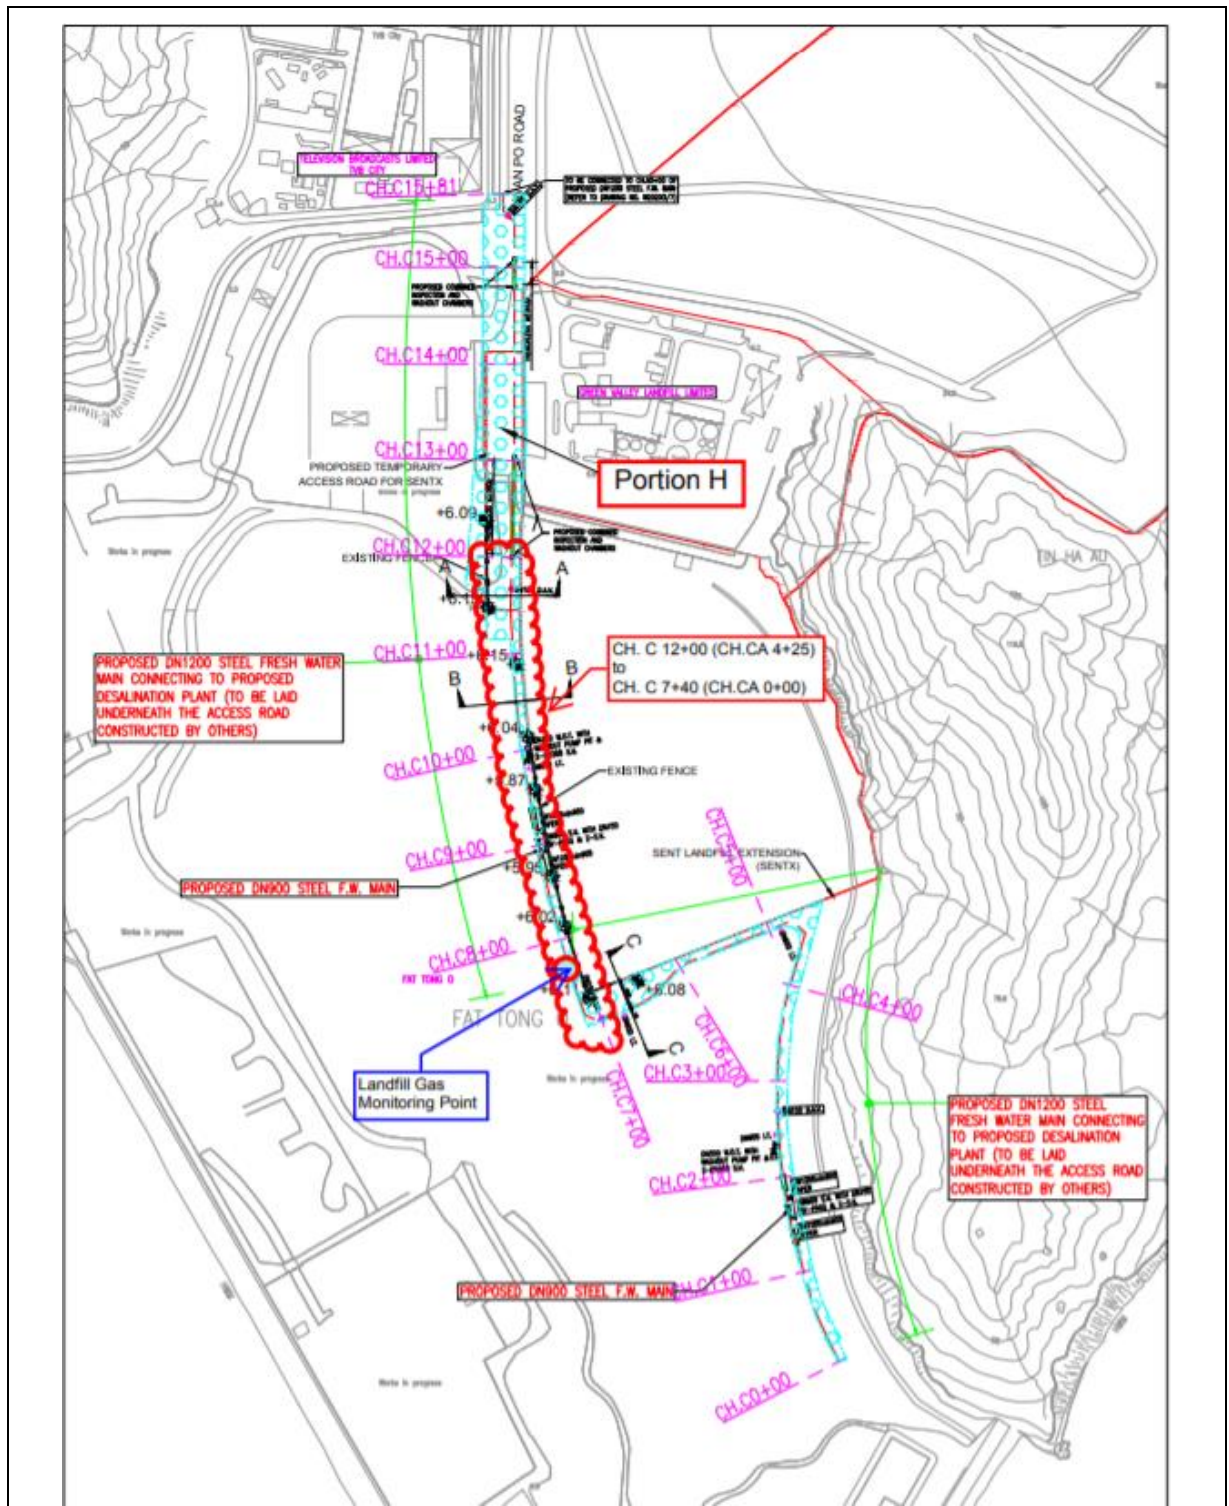


Figure 4.7 Monitoring Location –CH.CA 0+00 to CH.CA 04+25 (CH.C 7+40 ~ 12+00)

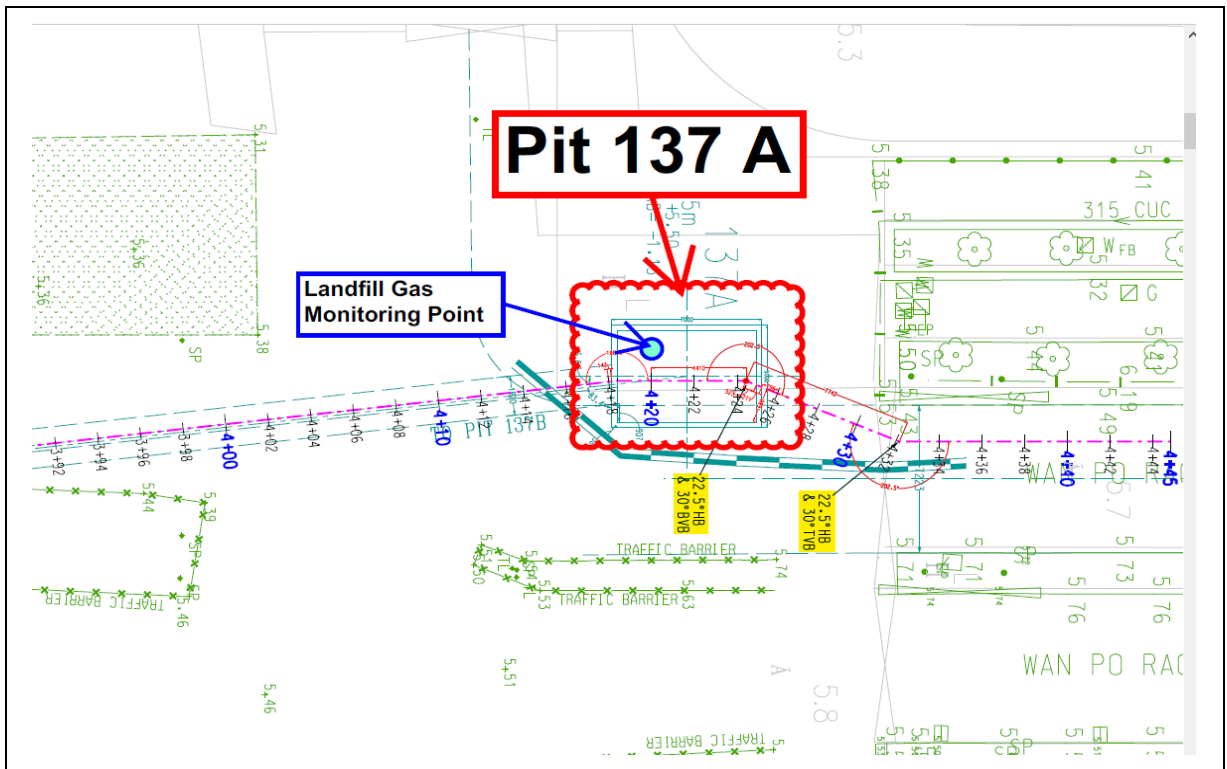


Figure 4.8a Monitoring Location – Pit 137A (137 Pit A)

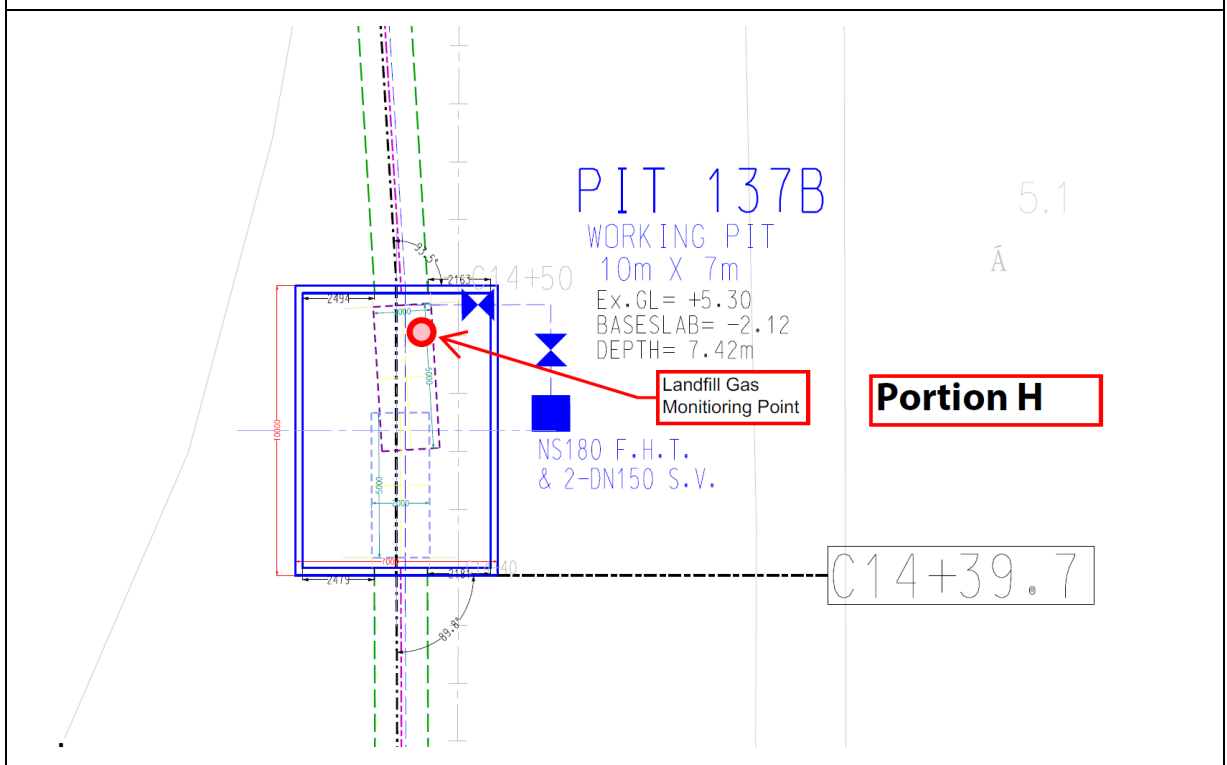


Figure 4.8b Monitoring Location – Pit 137B (137 Pit B)

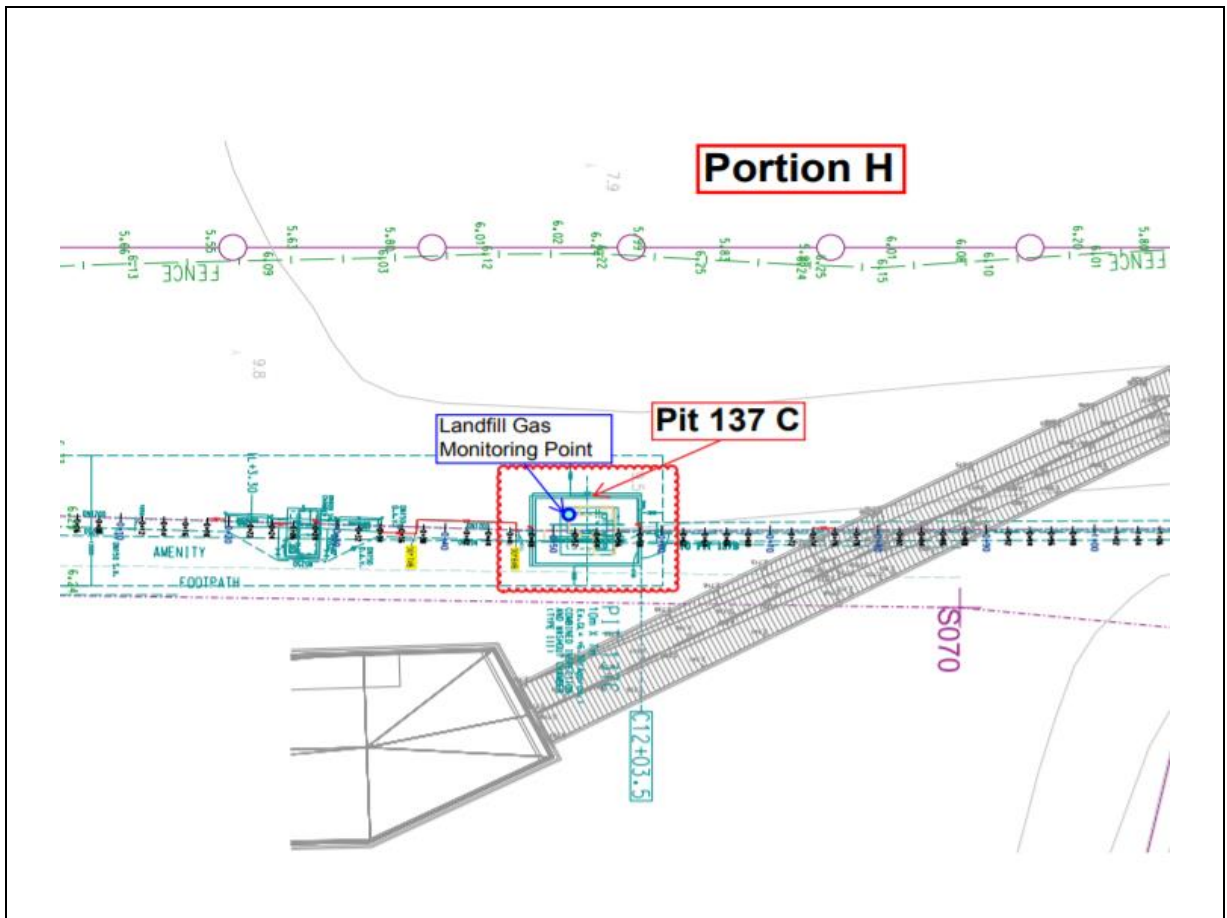


Figure 4.8c Monitoring Location – Pit 137C (137 Pit C)

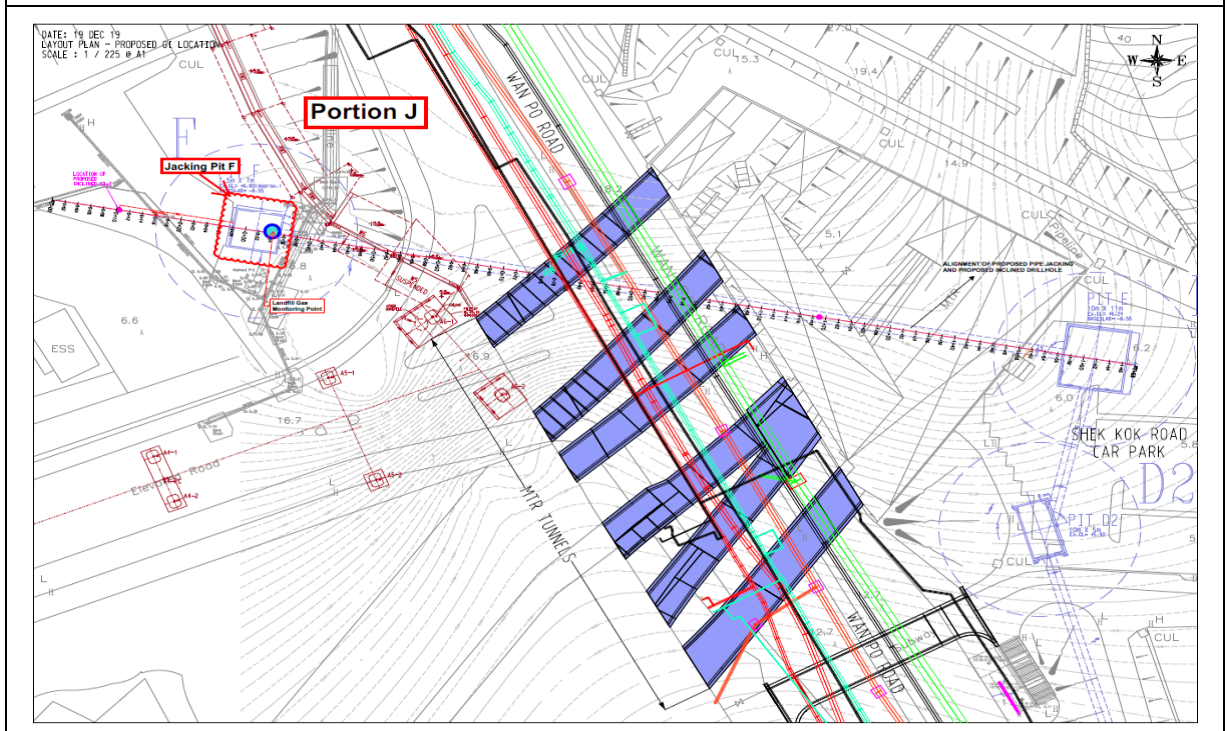


Figure 4.9 Monitoring Location – Jacking Pit F

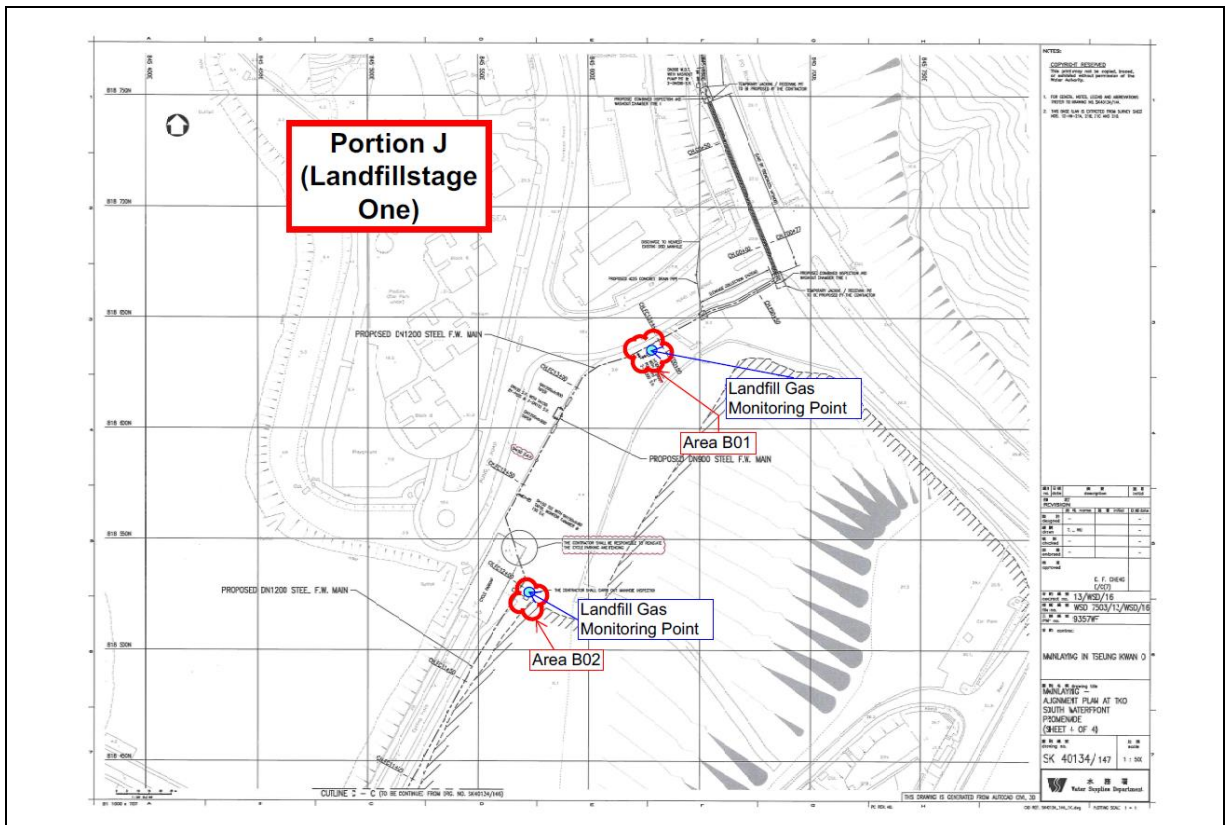


Figure 4.10a Monitoring Location – Landfill Stage 1 (Area B01-B02)

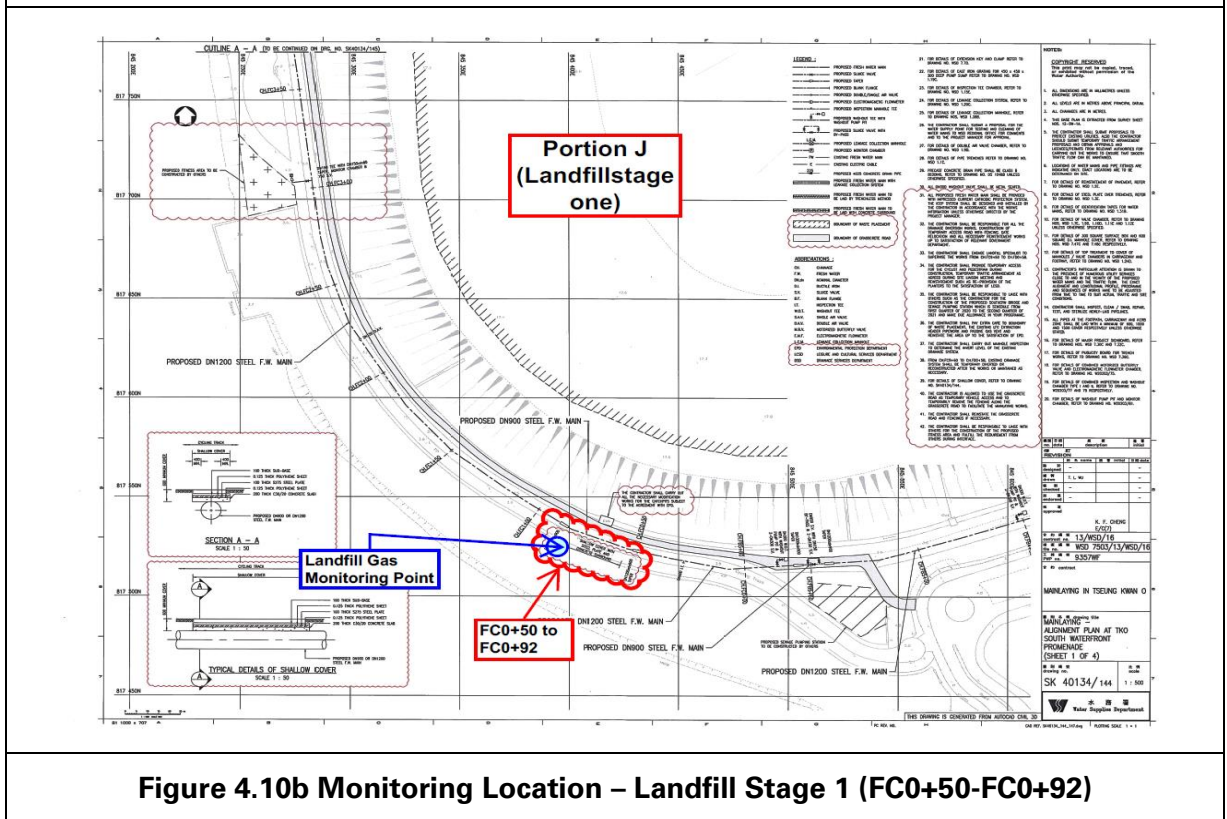


Figure 4.10b Monitoring Location – Landfill Stage 1 (FC0+50-FC0+92)

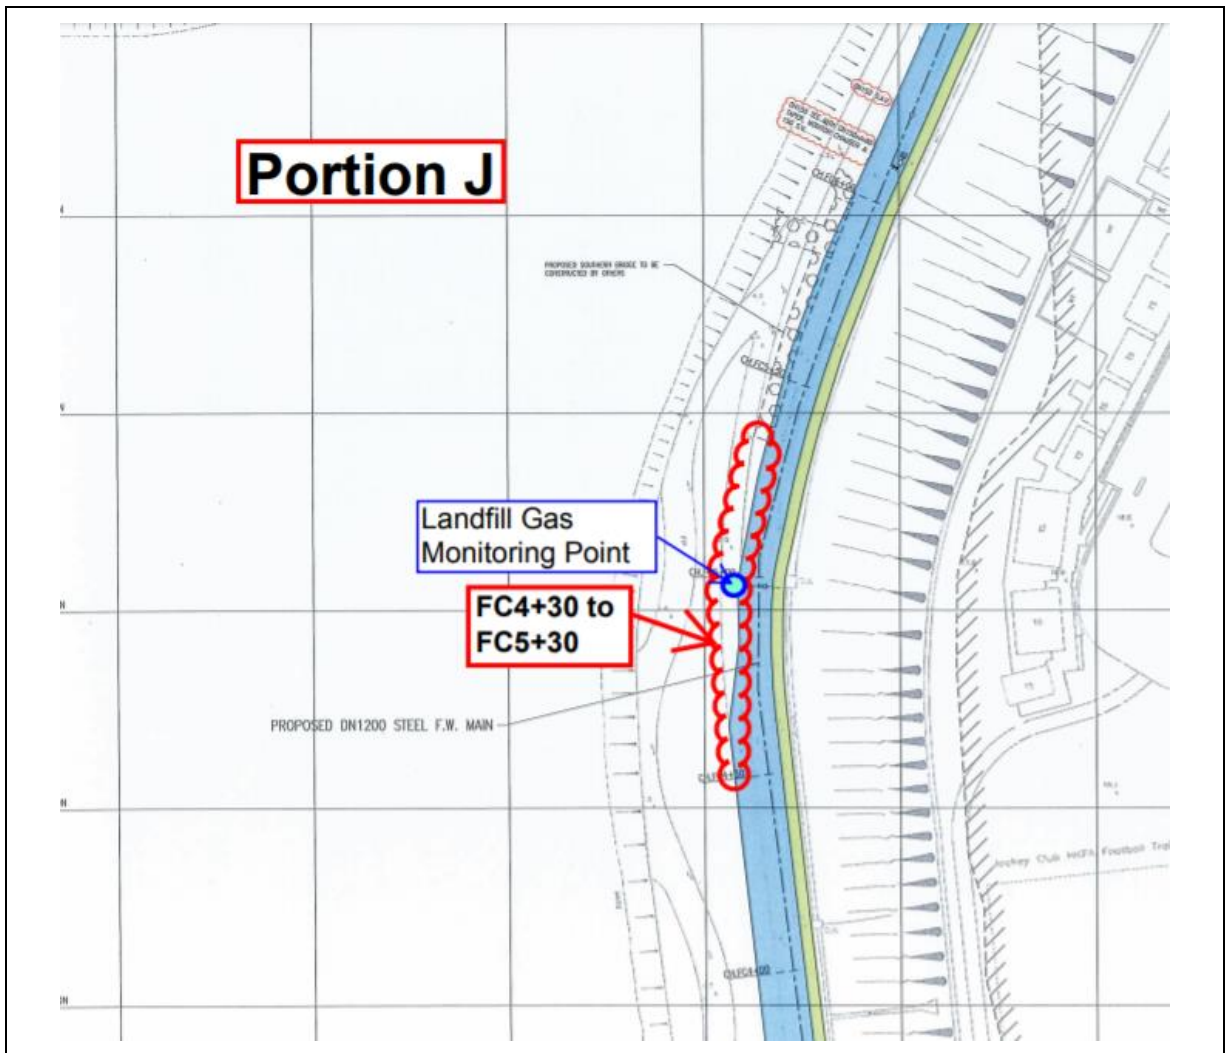


Figure 4.10c Monitoring Location – Landfill Stage 1 (FC4+30-FC5+30)

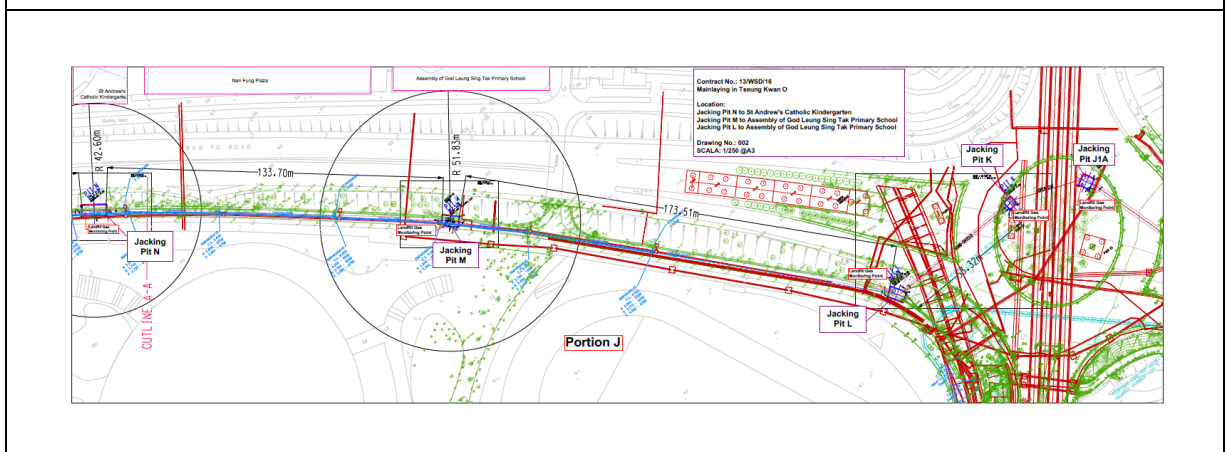


Figure 4.11a Monitoring Location – Pit L-M-N, J1A, K

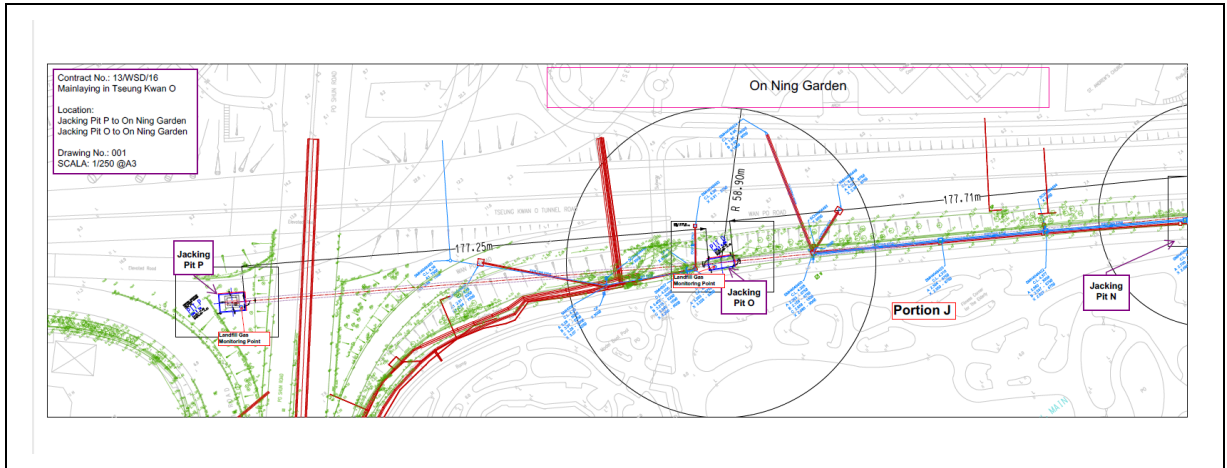


Figure 4.11b Monitoring Location – Pit N-O-P

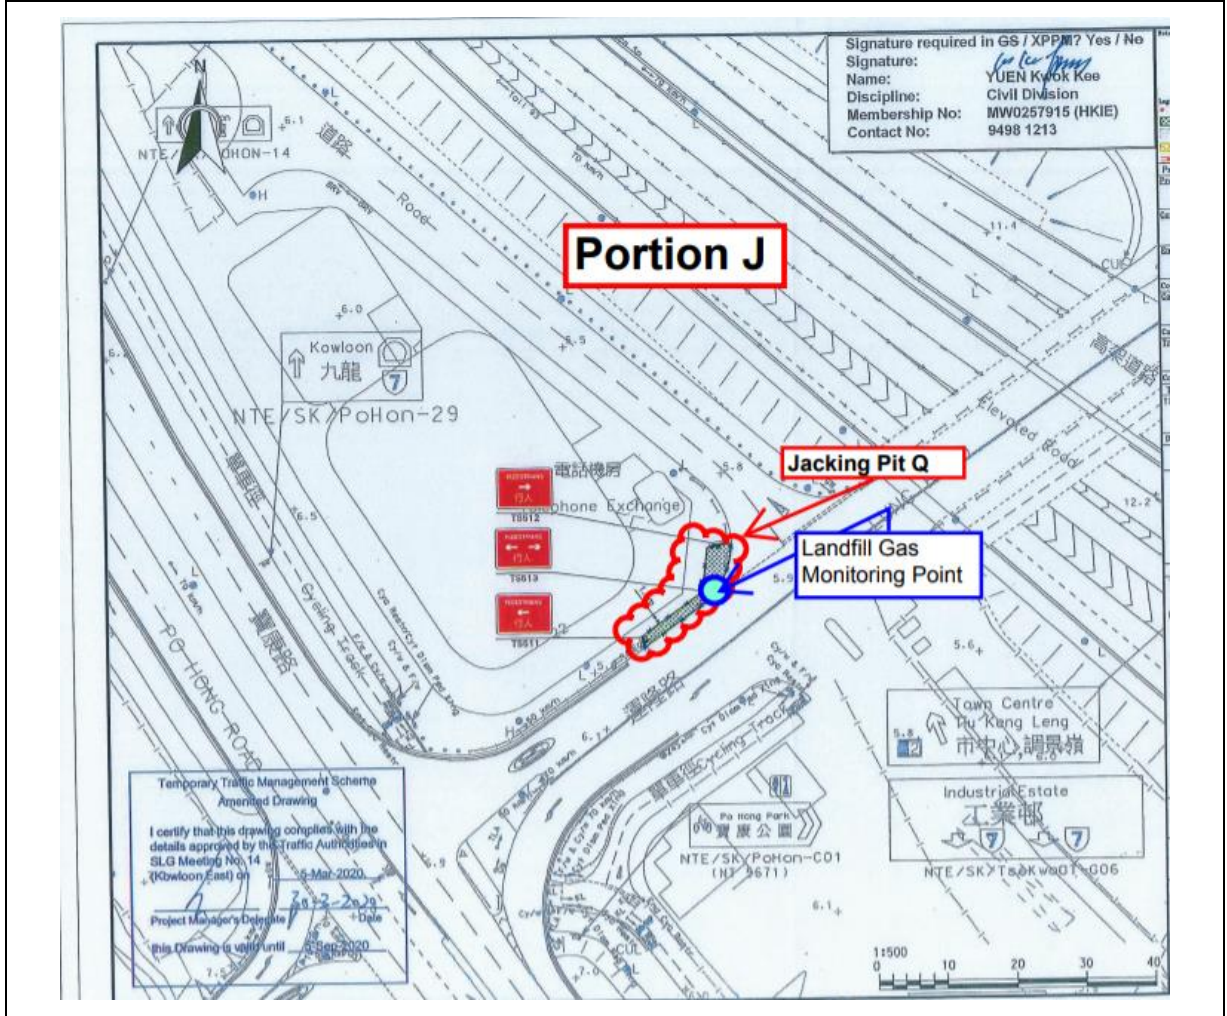


Figure 4.11c Monitoring Location – Pit Q

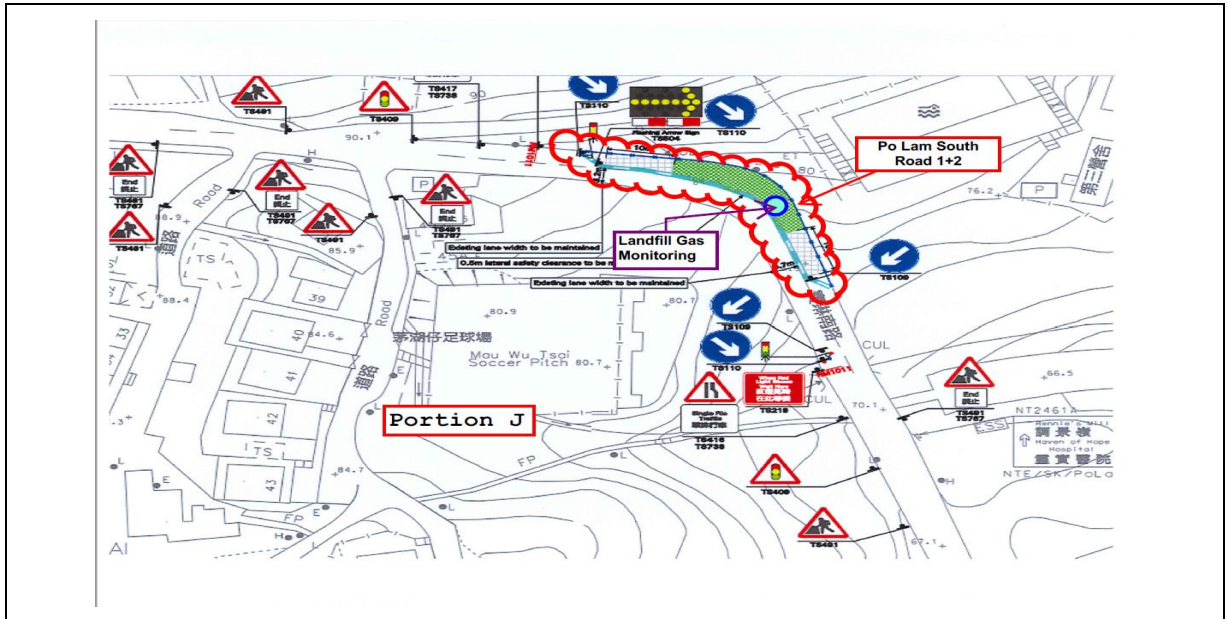


Figure 4.12 Po Lam South Road

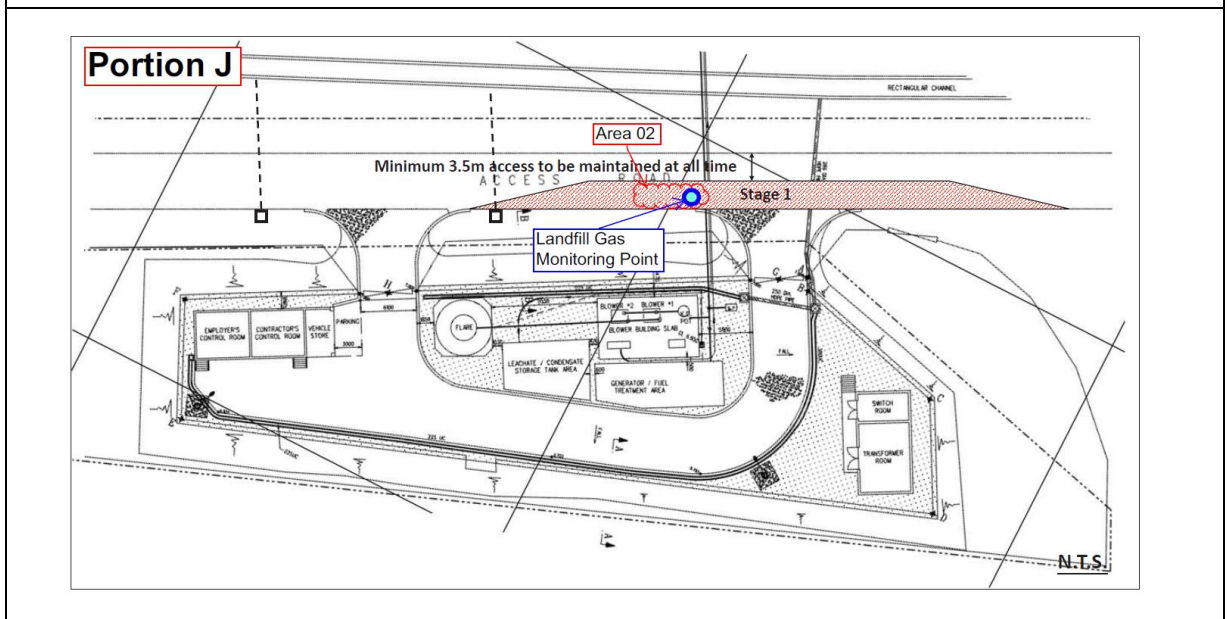


Figure 4.13 Monitoring Location – Area A02

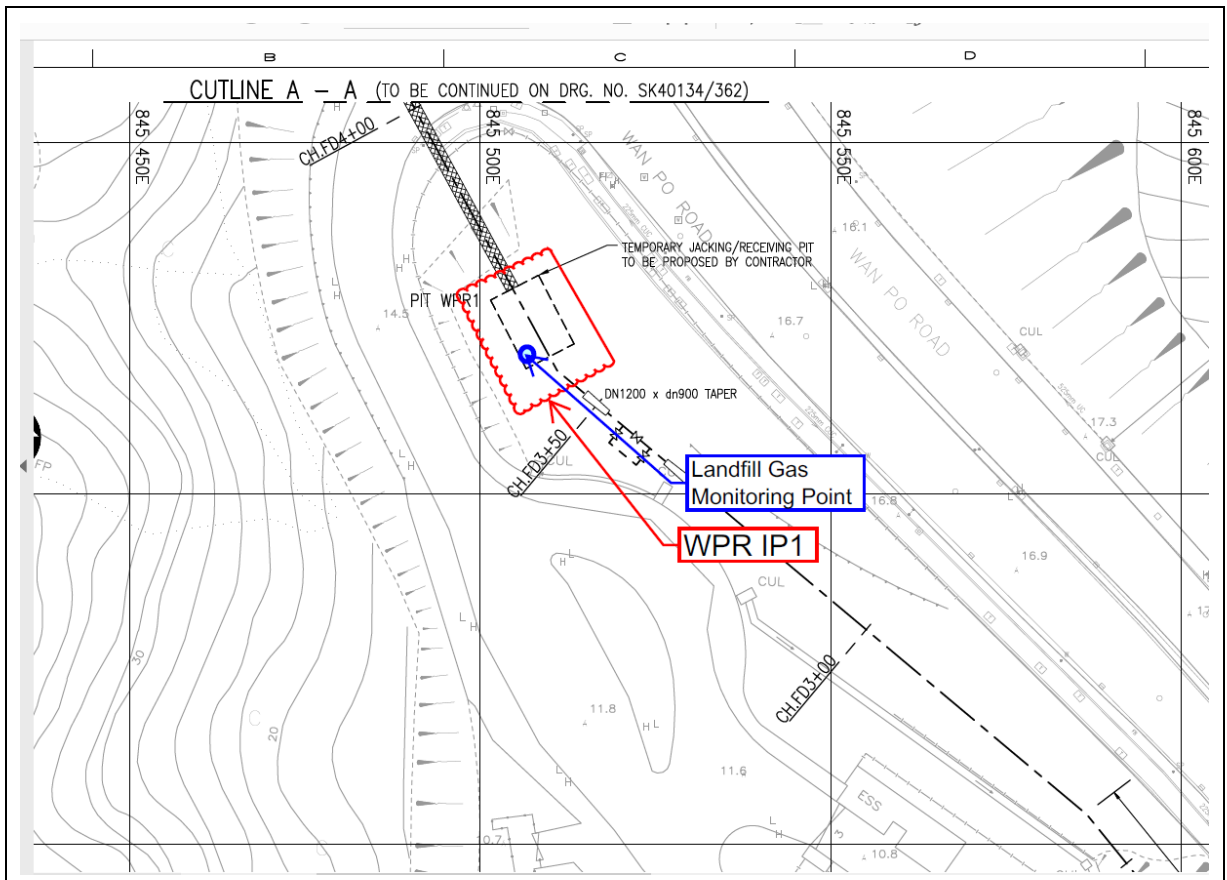


Figure 4.14 Monitoring Location – WPR IP1


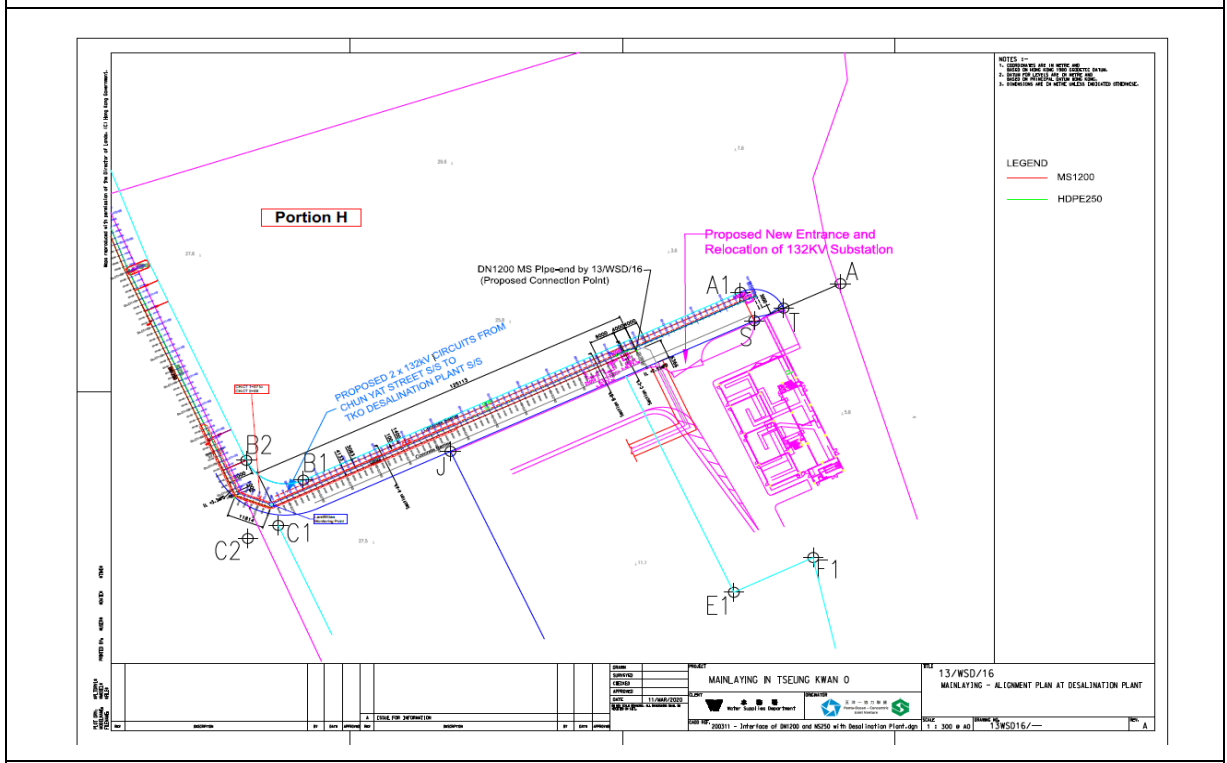


Figure 4.15a Monitoring Location - CH.CT 0+07 ~ 2+58

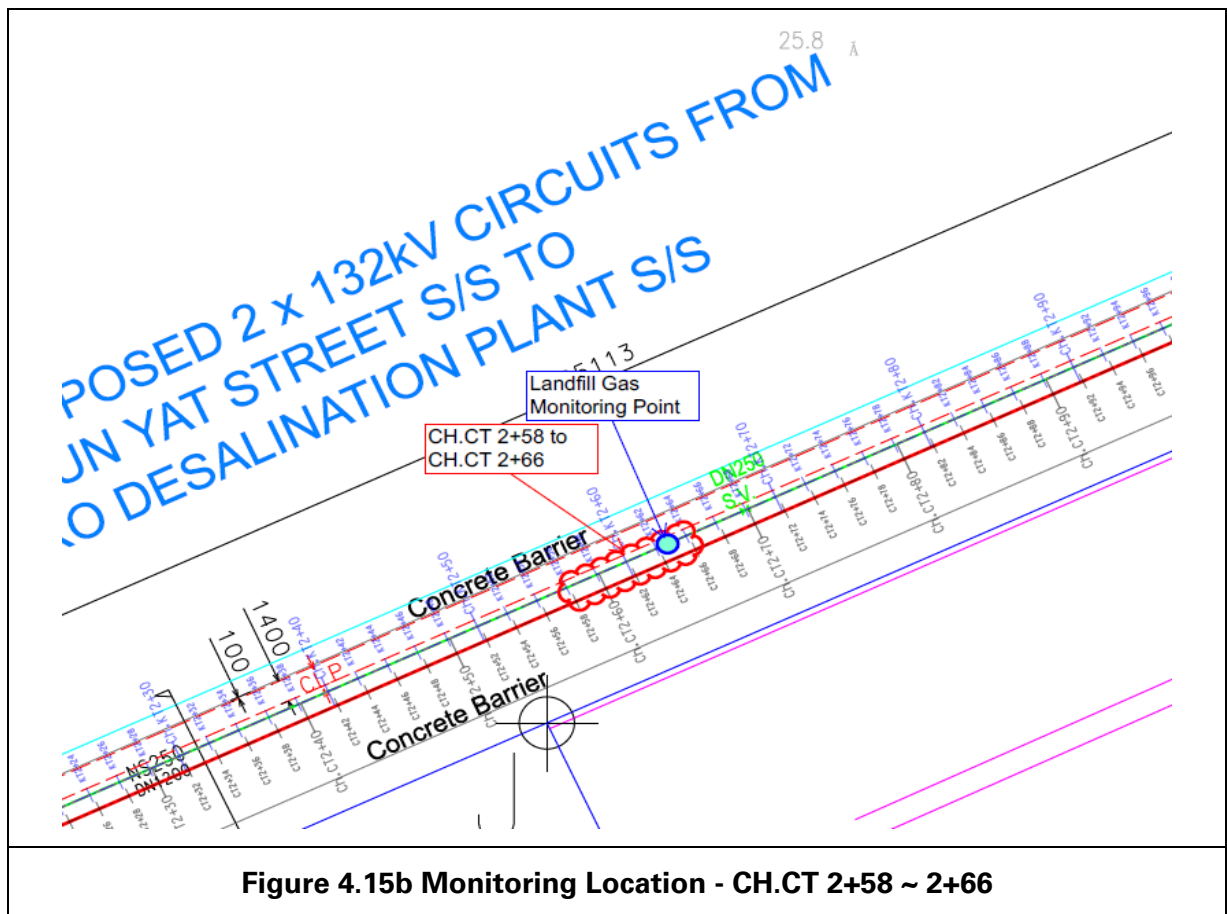

4.3 Monitoring Parameters

4.3.1 LFG monitoring was carried out to identify any migration between the landfill and the Project and to ensure the safety of the construction, operation and maintenance personnel working on-site, visitors and any other person within the Project area.

4.3.2 The following parameters were monitored:

- Methane.
- Oxygen.
- Carbon Dioxide.
- Barometric Pressure.

4.4 Action and Limit Level

4.4.1 Action and Limit Level are provided in **Table 4.1**.

Table 4.1 Action and Limit Level for Landfill Gas Monitoring Equipment

Parameters	Action Level	Limit Level
Oxygen (O ₂)	<19% O ₂	<19% O ₂
Methane (CH ₄)	>10% LEL	>80% LEL
Carbon Dioxide (CO ₂)	>0.5% CO ₂	>1.5% CO ₂

4.5 Monitoring Equipment

4.5.1 Landfill Gas monitoring was carried out using intrinsically-safe, portable multi-gas monitoring instruments. The gas monitoring equipment is:

- Comply with the Landfill Gas Hazard Assessment Guidance Note as intrinsically safe;
- Capable of continuous barometric pressure and gas pressure measurements;
- Normally operate in diffusion mode unless required for spot sampling, when it should be capable of operating by means of an aspirator or pump;
- Have low battery, fault and over range indication incorporated;
- Store monitoring data, and shall be capable of being down-loaded directly;
- Measure in the following ranges:

methane	0-100% Lower Explosion Limit (LEL) and 0-100% v/v;
oxygen	0-25% v/v;
carbon dioxide	0-100% v/v; and
barometric pressure	mBar (absolute)

- alarm (both audibly and visually) in the event that the concentrations of the following are exceeded:

methane	>10% LEL;
oxygen	<19% by volume; and
carbon dioxide	>0.5% by volume
barometric pressure	mBar (absolute)

4.5.2 Monitoring Equipment used in the reporting period are summarised in **Table 4.2**. The Landfill Gas monitoring equipment calibration certificate is presented in **Appendix I**.

Table 4.2 Landfill Gas Monitoring Equipment

Equipment	Brand and Model	Calibration Expiry Date
Portable Gas Detector	QRAE III	27 July 2021

4.6 Monitoring Results

4.6.1 In the reporting period, construction works within the consultation zones, excavations of 1m depth or more was monitored. Landfill gas monitoring was carried out by the Registered Safety Officer by the Contractor at the excavation locations for 706 times. All the measured results were presented in **Appendix J** and within the Action and Limit Levels.

5. SUMMARY OF MONITORING EXCEEDANCE, COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS

5.1 The Environmental Complaint Handling Procedure is shown in below **Figure 5.1:**

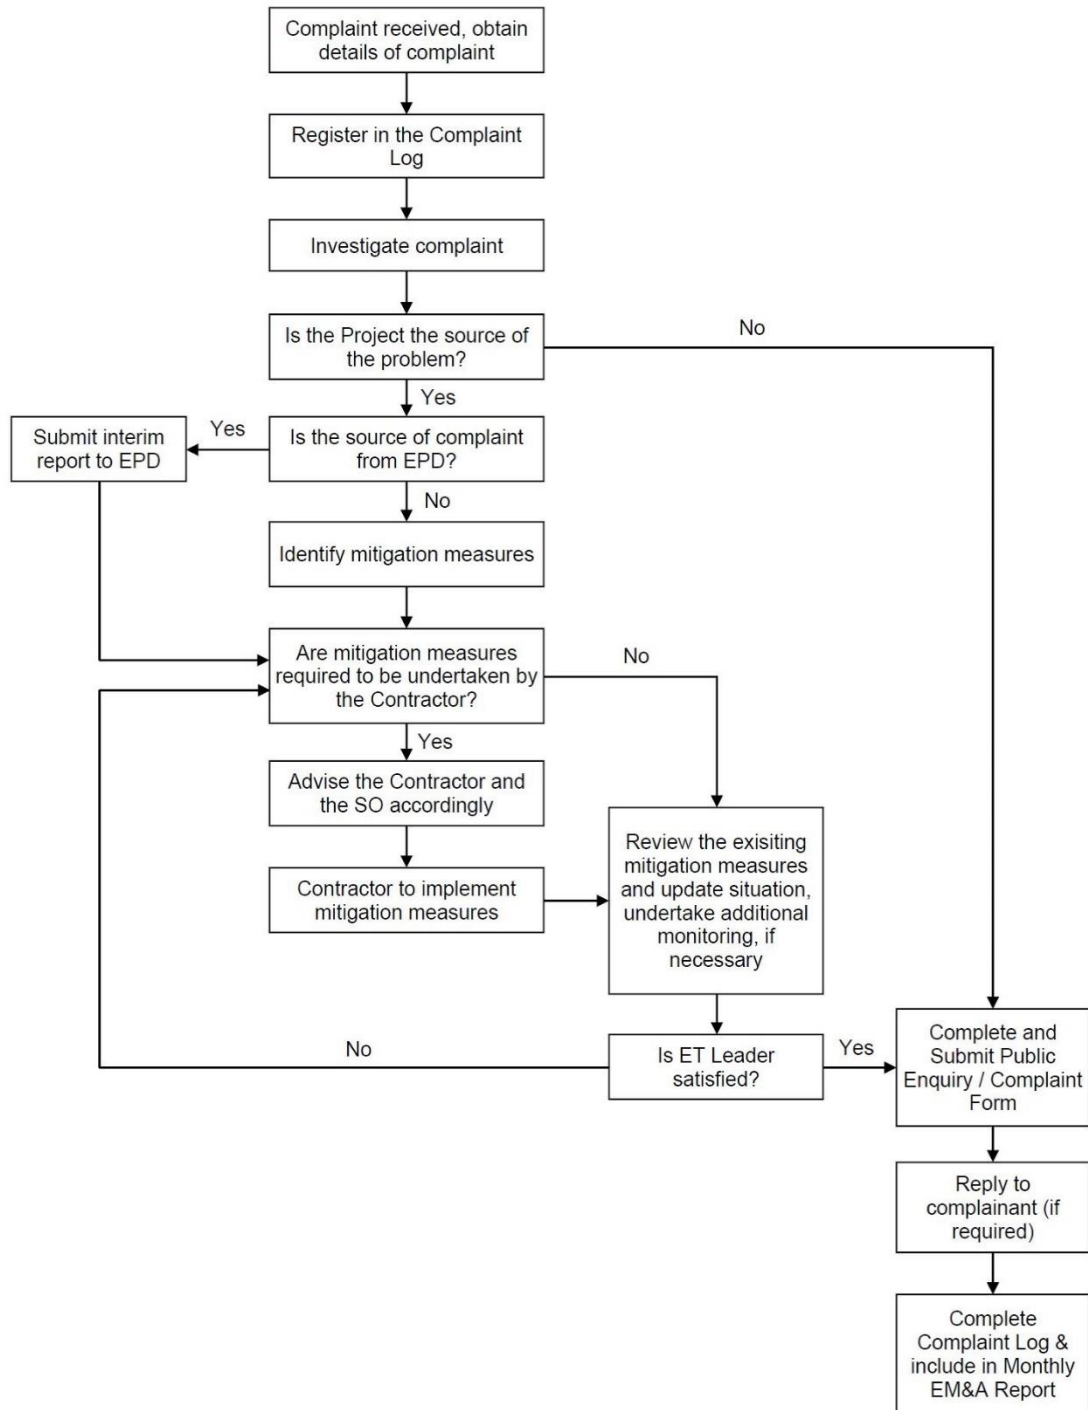


Figure 5.1 Environmental Complaint Handling Procedure

- 5.2 Impact monitoring for noise impact was conducted in the reporting month for NSR4 – Creative Secondary School on 6, 12, 18 and 27 November 2020 as construction works were conducted within 300m to the noise sensitive receiver. Detailed monitoring results can be found in **Appendix G**.
- 5.3 No project-related exceedance of the Action Level was recorded during the reporting period.
- 5.4 One noise related complaint was received in the reporting month on 15 November 2020 at Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T. After investigation with Contractor and confirmed by WSD, the works carried out on 15 November 2020 was an additional work under the same Work Contract 13/WSD/16 and the concerned work was not related to “a dedicated trunk feed system water minas for the transfer of fresh water output from the desalination plant to the existing Tsuen Kwan O Fresh Water Primary Service Reservoir in Po Lam”. The responsible contractor has been recommended, if any additional works to be carried in the future, should notify ET, Engineering Representative (i.e. WSD) and IEC of relevant method statements prior to commencement of the additional works for evaluation of sufficient and effective environmental mitigation measures and pollution controls to be taken for the additional works. The interim reports for the complaint is shown in Appendix P.
- 5.5 No notification of summons and prosecution was received in the reporting period.
- 5.6 Statistics on complaints and regulatory compliance are summarized in **Appendix K**.

6. EM&A SITE INSPECTION

- 6.1 Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, site inspections were carried out on 3, 12, 19 and 23 November at the site portions list in **Table 6.1** below.

Table 6.1 Site Inspection Record

Date	Inspected Site Portion	Time
03 November 2020	Portion J and H	9:32am – 11:00pm
12 November 2020	Portion J, F and H	9:40am – 12:20pm
19 November 2020	Portion F and J	9:30am – 12:00pm
23 November 2020	Portion J	9:30am – 12:00pm

- 6.2 One joint site inspection with IEC was carried out on 23 November 2020.
- 6.3 Minor deficiencies were observed during weekly site inspection. Key observations during the site inspections are summarized in **Table 6.2**.

Table 6.2 Site Observations

Date	Environmental Observations	Follow-up Status
03 November 2020	<ol style="list-style-type: none"> 1. NRMM label was not observed on the NRMM at 137 Pit C. 2. Stored stockpile of dusty materials should be sprayed with water and covered with tarpaulin sheet at CHA12+50. 	<ol style="list-style-type: none"> 1. NRMM label was added. 2. Stored stockpile of dusty materials was cleaned.
12 November 2020	<ol style="list-style-type: none"> 1. Chemicals were not placed inside a drip tray at Portion F. 	<ol style="list-style-type: none"> 1. Chemicals were placed inside a drip tray.
19 November 2020	<ol style="list-style-type: none"> 1. Chemicals were not placed inside a drip tray at Portion F. 2. Dusty materials were observed at the site entrance/exit at Jacking Pit C. 3. Construction boundary was not protected by sandbags at CHA6+64. 4. Gully was not protected by sandbags at CHA6+64 and CHA12+50. 5. Wastewater was not treated before discharge at CHA12+50. 	<ol style="list-style-type: none"> 1. Chemicals were removed. 2. Dusty materials were cleaned. 3. Construction boundary was protected by sandbags. 4. Gully was protected. 5. Wastewater was treated before discharge.
23 November 2020	<ol style="list-style-type: none"> 1. Oil spillage was found at Pit L at Hong Kong Velodrome. 	<ol style="list-style-type: none"> 1. Oil spillage was cleaned.

6.4 According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents should be implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix C**.

6.5 Site inspection proforma of the reporting period is provided in **Appendix L**.

7. FUTURE KEY ISSUES

7.1 Key works that will be anticipated in the next reporting period for the Project are shown in **Table 7.1**.

Table 7.1. Key works for the next reporting month

Location	Location	Forecast Works for November 2020
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> Preparation works and hydrostatic pressure testing for completed MS1200 pipeline section will be conducted.
	TKO 137 Pit A	<ul style="list-style-type: none"> Pit ELS and excavation works will be continued.
	TKO 137 Pit B	<ul style="list-style-type: none"> Pit ELS and excavation works will be continued.
	TKO 137 Pit C	<ul style="list-style-type: none"> Pit pipe piling for ELS works will be continued.
Portion J of the Project Site	Wan Po Rd – Workfront 1	<ul style="list-style-type: none"> Trench excavation and pipe laying will be conducted.
	Wan Po Rd – Workfront 2	<ul style="list-style-type: none"> Trench excavation and pipe laying works will be conducted. Road reinstatement and TTA shifting to next stage will be conducted.
	Wan Po Rd – Workfront 3	<ul style="list-style-type: none"> Construction for IT chamber will be continued. Trench excavation and mainlaying works will be conducted.
	Wan Po Rd – Pit A	<ul style="list-style-type: none"> Excavation and ELS works will be conducted.
	Wan Po Rd – Pit B	N/A
	Wan Po Rd – Pit C	N/A
	Landfill Stage 1 – Area A	<ul style="list-style-type: none"> Trench excavation and pipe laying works will be conducted.
	Landfill Stage 1 – Area B	<ul style="list-style-type: none"> Trench excavation and pipe laying works will be conducted.
	Cycle Track – Workfront 1	<ul style="list-style-type: none"> Trench excavation and pipe laying works will be conducted.
	Cycle Track – Workfront 2	<ul style="list-style-type: none"> Trench excavation and pipe laying works will be conducted.
	Velodrome – Pit L	<ul style="list-style-type: none"> Pit excavation will be conducted.
	Velodrome – Pit M	<ul style="list-style-type: none"> Pipe jacking works will be continued.
	Velodrome – Pit N	N/A
	Velodrome – Pit O	<ul style="list-style-type: none"> Establishment for pipe jacking works will be completed.
Velodrome – Pit P	<ul style="list-style-type: none"> Grouting works will be completed. Pit excavation and ELS works will be resumed 	

Location	Location	Forecast Works for November 2020
	Mau Wu Tsai	<ul style="list-style-type: none"> Trench excavation and pipe mainlaying works will be conducted.

7.2 The major environmental impacts brought by the above construction works will include:

- Construction dust and noise generation of saw cutting of concrete surface, mainlaying of pipes, pipe piling, grouting, excavation works and installation works.
- Waste generation from construction activities

7.3 The key environmental mitigation measures for the Project in the coming reporting period associated with the above construction works will include:

- Dust suppression by regular wetting and water spraying for saw cutting of concrete surface, mainlaying of pipes, pipe piling, grouting, excavation works and installation works
- Reduction of noise from equipment and machinery on-site
- Sorting and storage of general refuse and construction waste

7.4 The proactive environmental protection proforma for the next reporting month is listed in **Appendix M**.

7.5 Referring to EM&A Manual Section 4.1.2, the impact noise monitoring should be carried out at all the designated monitoring stations when there are project-related construction activities undertaken within a radius of 300m from the monitoring stations.

7.6 The tentative impact monitoring schedule for the next reporting month is attached in **Appendix N**.

8. CONCLUSION AND RECOMMENDATIONS

- 8.1 This is the 28th monthly Environmental Monitoring and Audit (EM&A) Report presenting the EM&A works undertaken during the period from 1 November 2020 to 30 November 2020, in accordance with the EM&A Manual and the requirement under EP-503/2015/A.
- 8.2 Impact monitoring for noise impact was conducted in the reporting month for NSR4 – Creative Secondary School on 6, 12, 18 and 27 November 2020 as construction works were conducted within 300m to the noise sensitive receiver. Detailed monitoring results can be found in **Appendix G**.
- 8.3 No project-related exceedance of the Action Level was recorded during the reporting period.
- 8.4 Weekly environmental site inspection was conducted during the reporting period. Minor deficiencies were observed during site inspection and were rectified. The environmental performance of the project was therefore considered satisfactory.
- 8.5 According to the environmental site inspections performed in the reporting month, the contractor is reminded to pay attention on maintaining site tidiness, water treatment facilities, dust suppression mitigations and proper materials storage.
- 8.6 One noise related complaint was received in the reporting month on 15 November 2020 at Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T. After investigation with Contractor and confirmed by WSD, the works carried out on 15 November 2020 was an additional work under the same Work Contract 13/WSD/16 and the concerned work was not related to “a dedicated trunk feed system water minas for the transfer of fresh water output from the desalination plant to the existing Tsuen Kwan O Fresh Water Primary Service Reservoir in Po Lam”. The responsible contractor has been recommended, if any additional works to be carried in the future, should notify ET, Engineering Representative (i.e. WSD) and IEC of relevant method statements prior to commencement of the additional works for evaluation of sufficient and effective environmental mitigation measures and pollution controls to be taken for the additional works. The interim reports for the complaint is shown in Appendix P.
- 8.7 No notification of summons or prosecution was received since the commencement of the Contract.
- 8.8 The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Appendix A

Construction Programme

Appendix B

Overview of Mainlaying in Tseung Kwan O

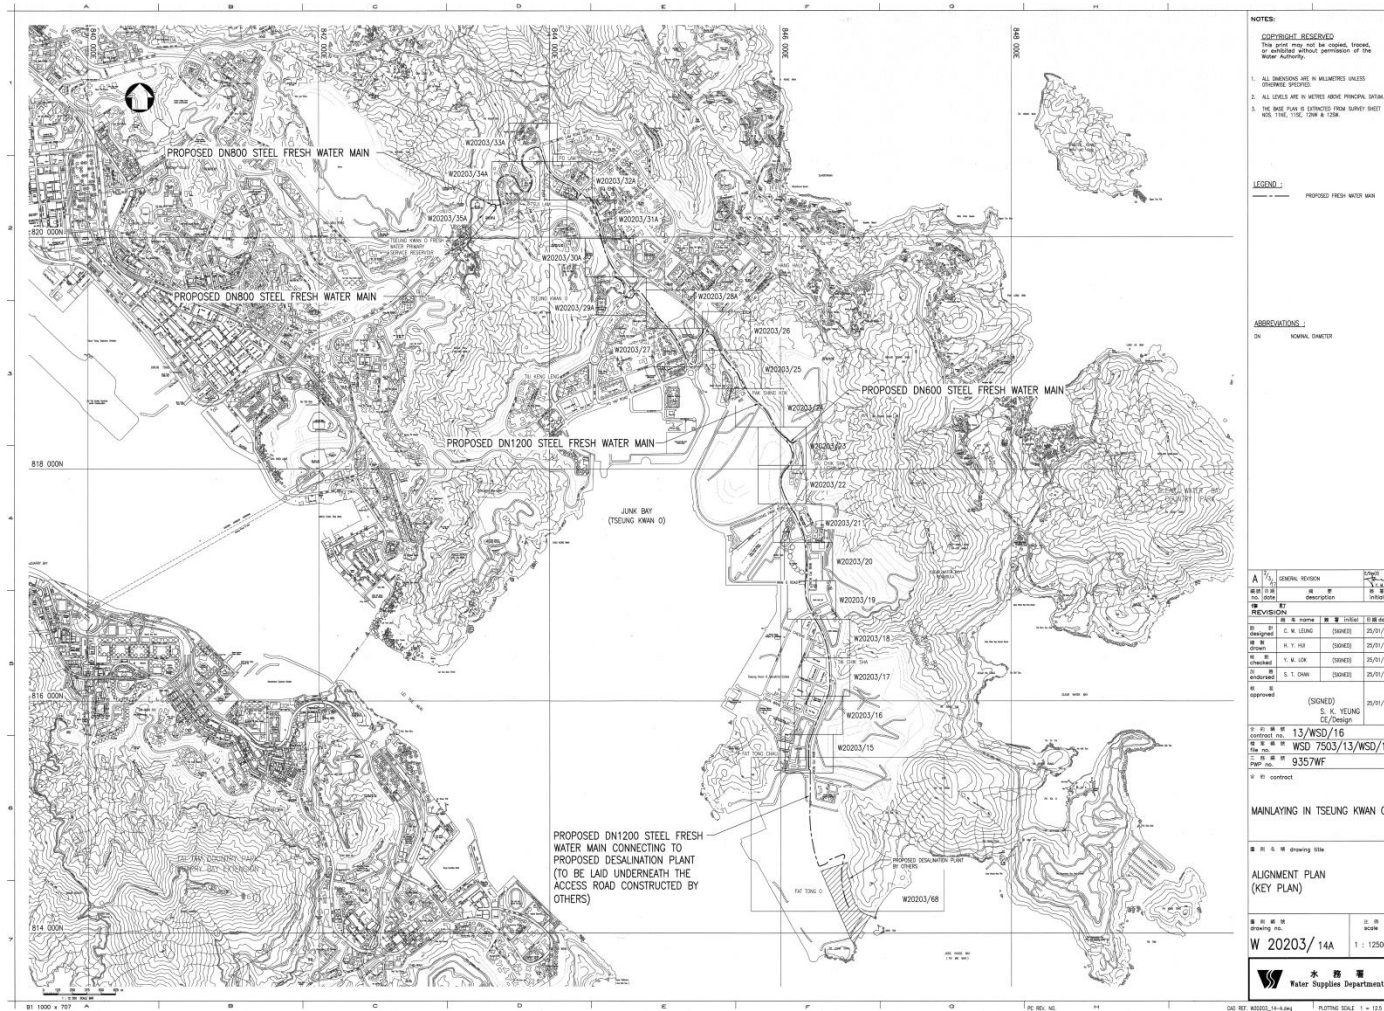


Figure B1. Overview of Mainlaying in TKO

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28


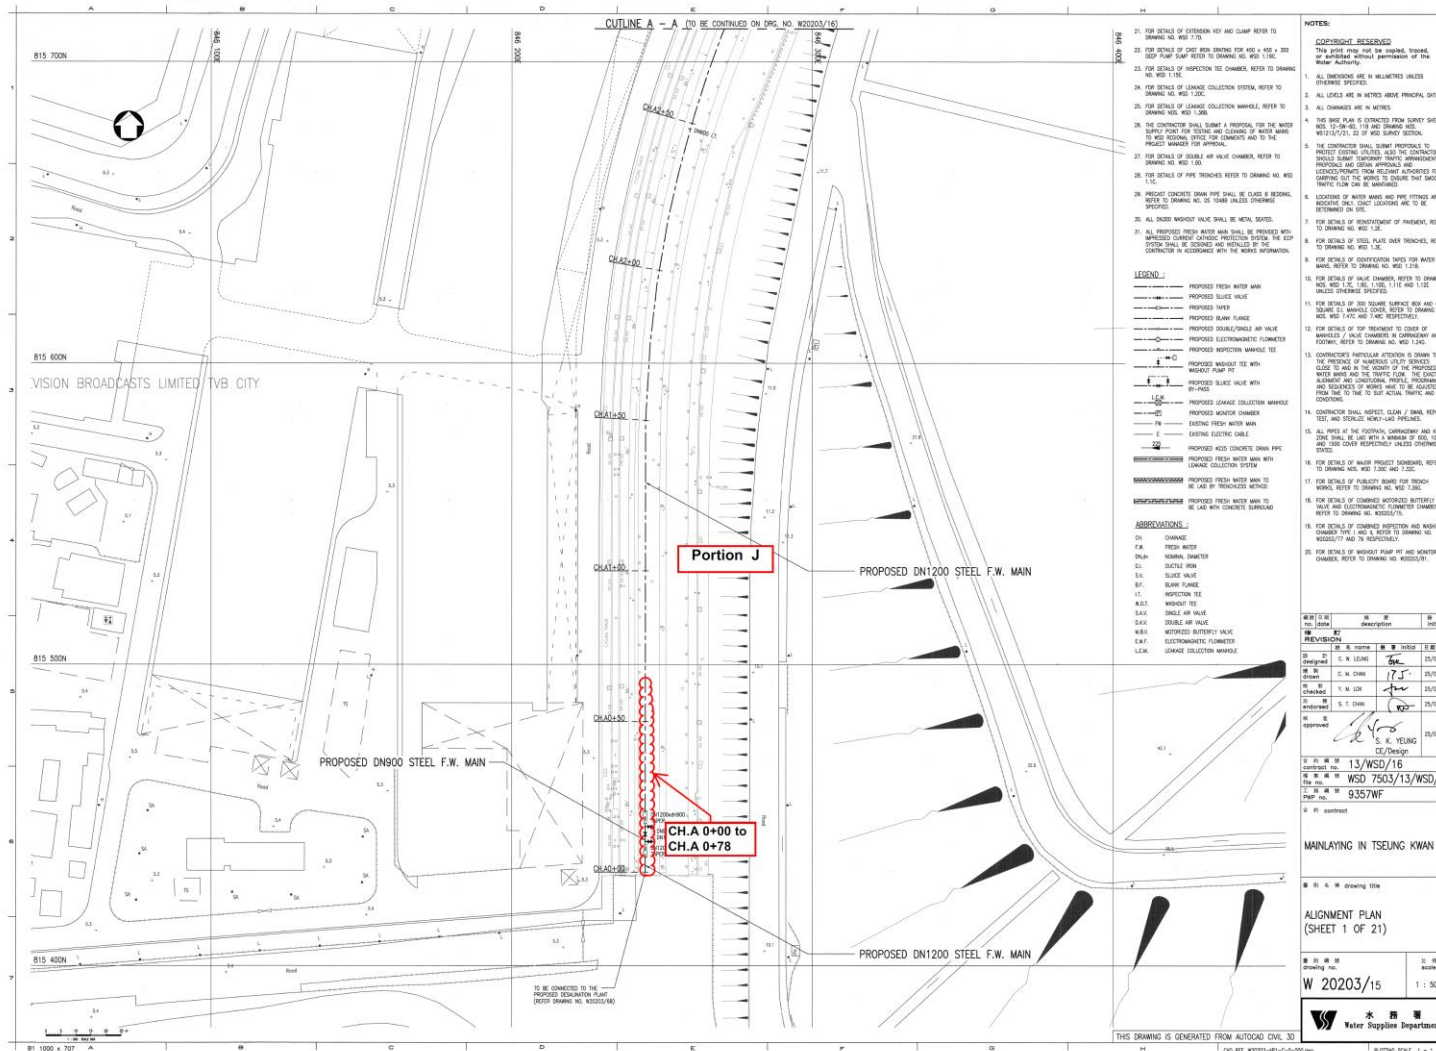


Figure B2. Location Plan for Portion J - CH.A 0+00 to CH.A 0+78

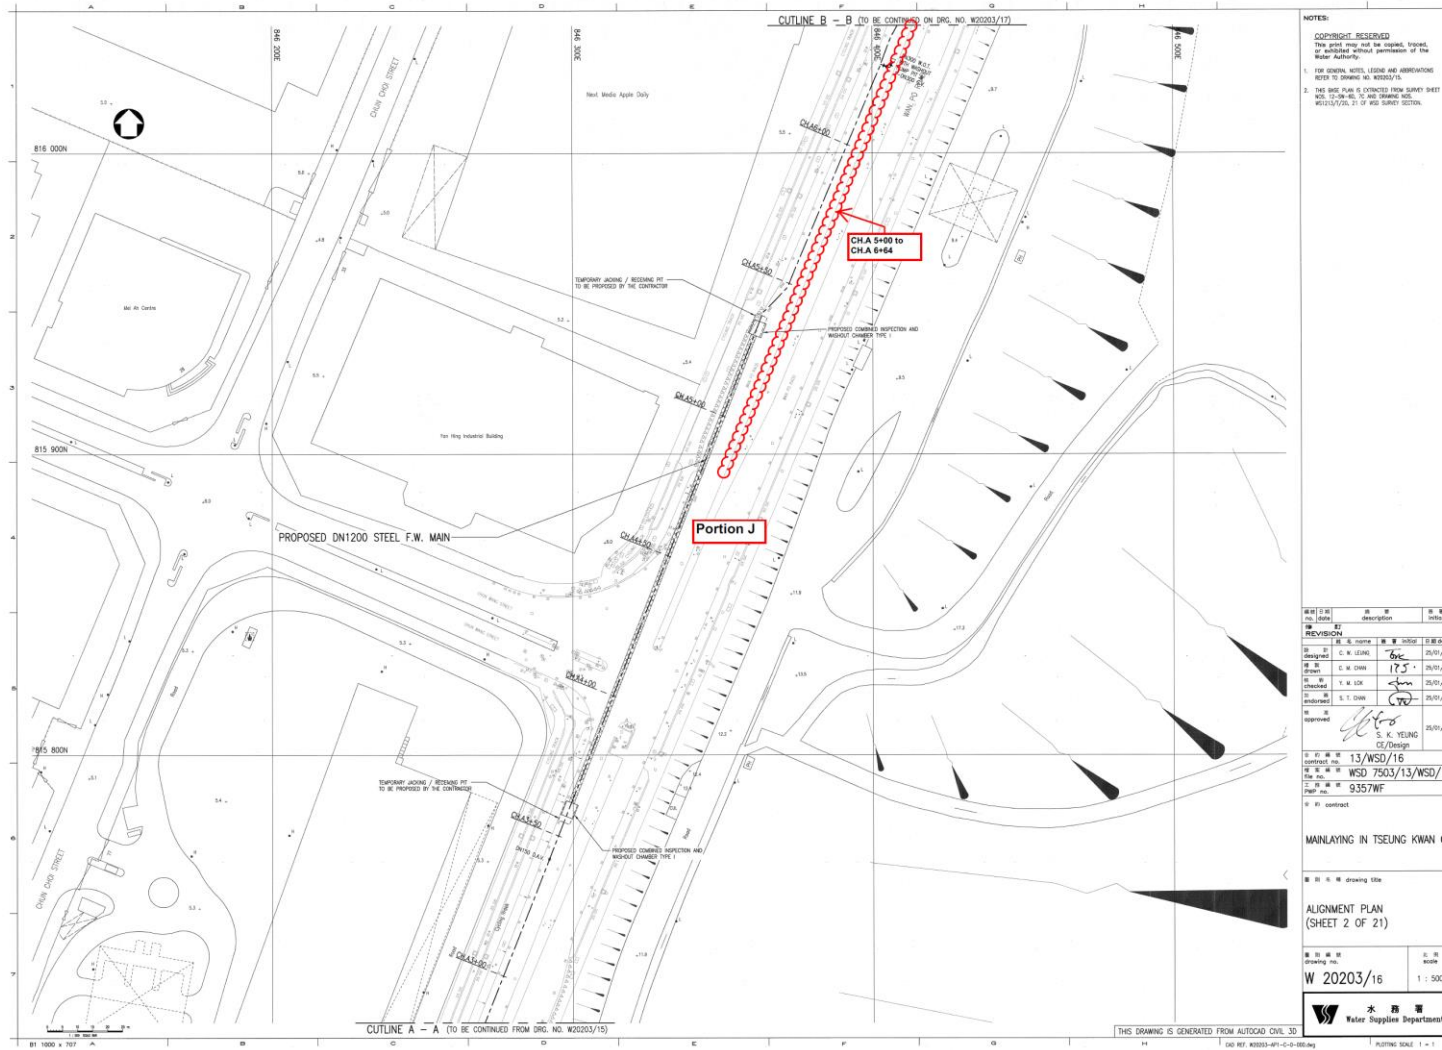

NOTES:

COPYRIGHT RESERVED
 The work shown shall be copied, copied, or reproduced without permission of the Water Authority.

1. FOR DIMENSIONS, NOTES, LEGEND AND ABBREVIATIONS REFER TO DRAWING NO. W20203/15.

2. THIS SHEET PLAN IS EXTRACTED FROM SURVEY SHEET NO. 13-20-46, 15-40, 16-30, 16-40, 16-50, 16-60, 16-70, 16-80, 16-90, 16-100, 16-110, 16-120, 16-130, 16-140, 16-150, 16-160, 16-170, 16-180, 16-190, 16-200, 16-210, 16-220, 16-230, 16-240, 16-250, 16-260, 16-270, 16-280, 16-290, 16-300, 16-310, 16-320, 16-330, 16-340, 16-350, 16-360, 16-370, 16-380, 16-390, 16-400, 16-410, 16-420, 16-430, 16-440, 16-450, 16-460, 16-470, 16-480, 16-490, 16-500, 16-510, 16-520, 16-530, 16-540, 16-550, 16-560, 16-570, 16-580, 16-590, 16-600, 16-610, 16-620, 16-630, 16-640, 16-650, 16-660, 16-670, 16-680, 16-690, 16-700, 16-710, 16-720, 16-730, 16-740, 16-750, 16-760, 16-770, 16-780, 16-790, 16-800, 16-810, 16-820, 16-830, 16-840, 16-850, 16-860, 16-870, 16-880, 16-890, 16-900, 16-910, 16-920, 16-930, 16-940, 16-950, 16-960, 16-970, 16-980, 16-990, 16-1000.

REV.	NO.	DATE	DESCRIPTION	BY	CHECKED
1	1	20/9/17	ISSUED FOR TENDER	C. W. JENNY	S. K. YELING
2	2	20/9/17	DESIGNED	C. W. JENNY	S. K. YELING
3	3	20/9/17	DRAWN	S. K. YELING	S. K. YELING
4	4	20/9/17	CHECKED	S. K. YELING	S. K. YELING
5	5	20/9/17	APPROVED	S. K. YELING	S. K. YELING


DESIGNED BY: C. W. JENNY
 DRAWN BY: S. K. YELING
 CHECKED BY: S. K. YELING
 APPROVED BY: S. K. YELING

PROJECT NO: 13/WSD/16
 CONTRACT NO: WSD 7503/13/WSD/16
 DRAWING NO: 9357WF
 SHEET NO: 2 OF 21

SCALE: 1 : 500

WATER SUPPLY DEPARTMENT

Figure B3a. Location Plan for Portion J - CH.A 5+00 to CH.A 6+64

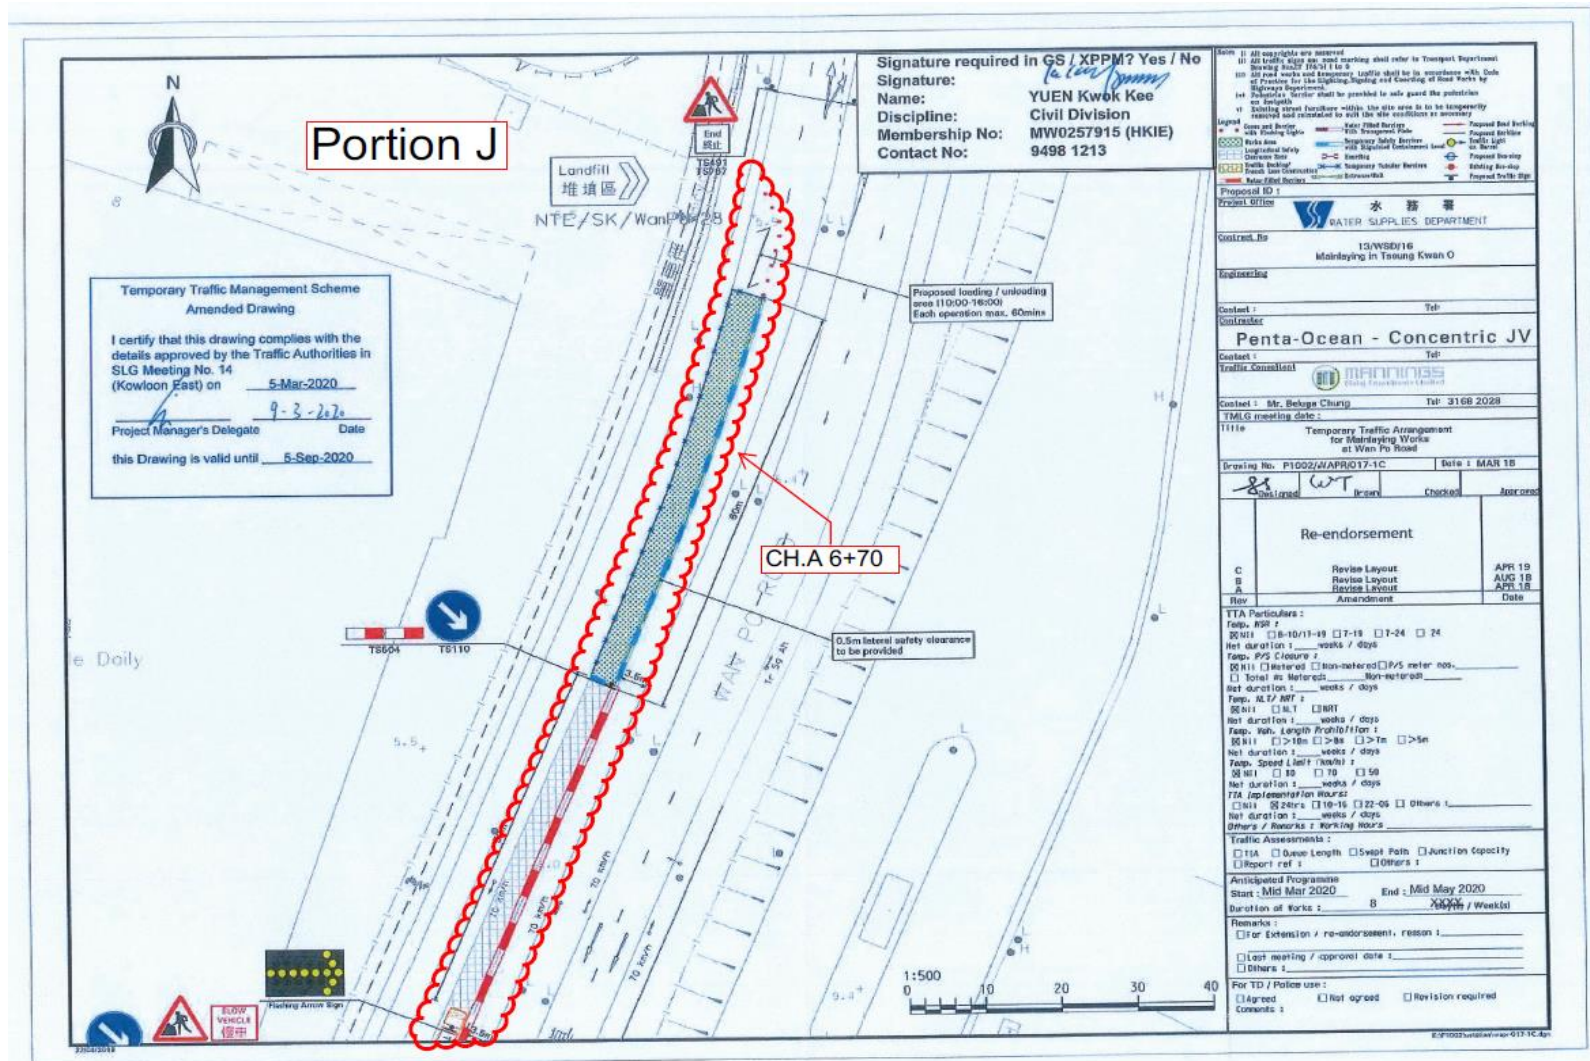


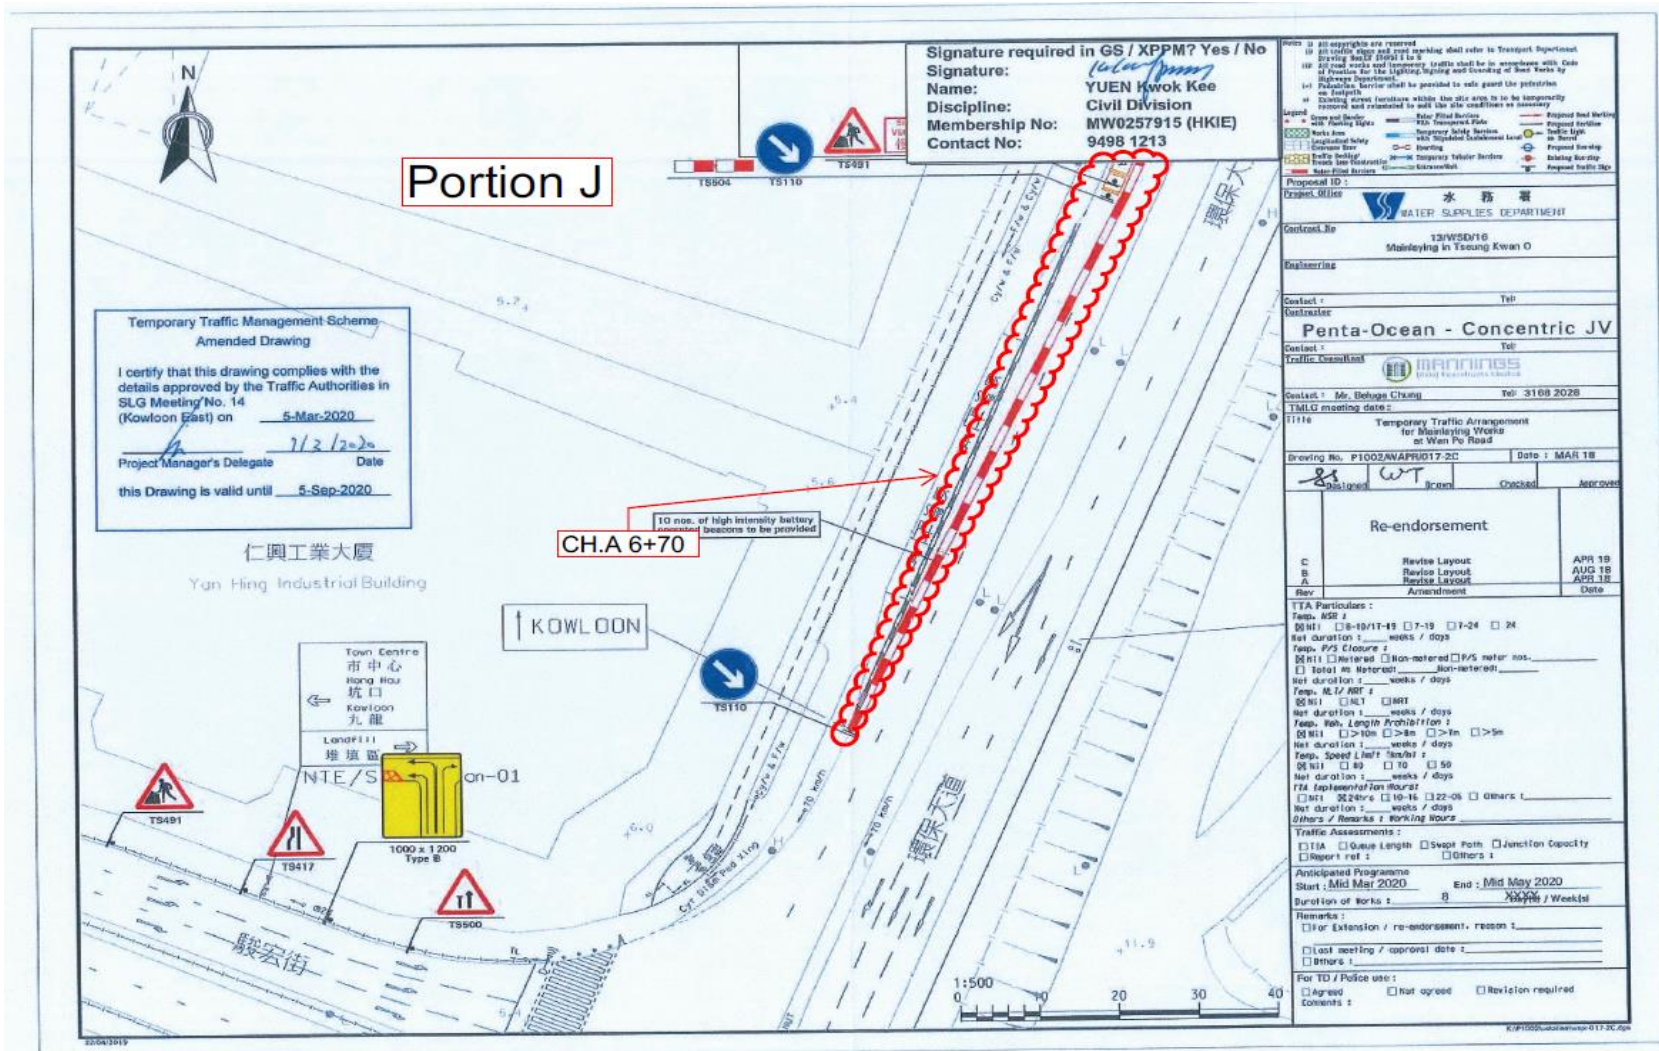


Figure B3b. Location Plan for Portion J - CH.A 6+70

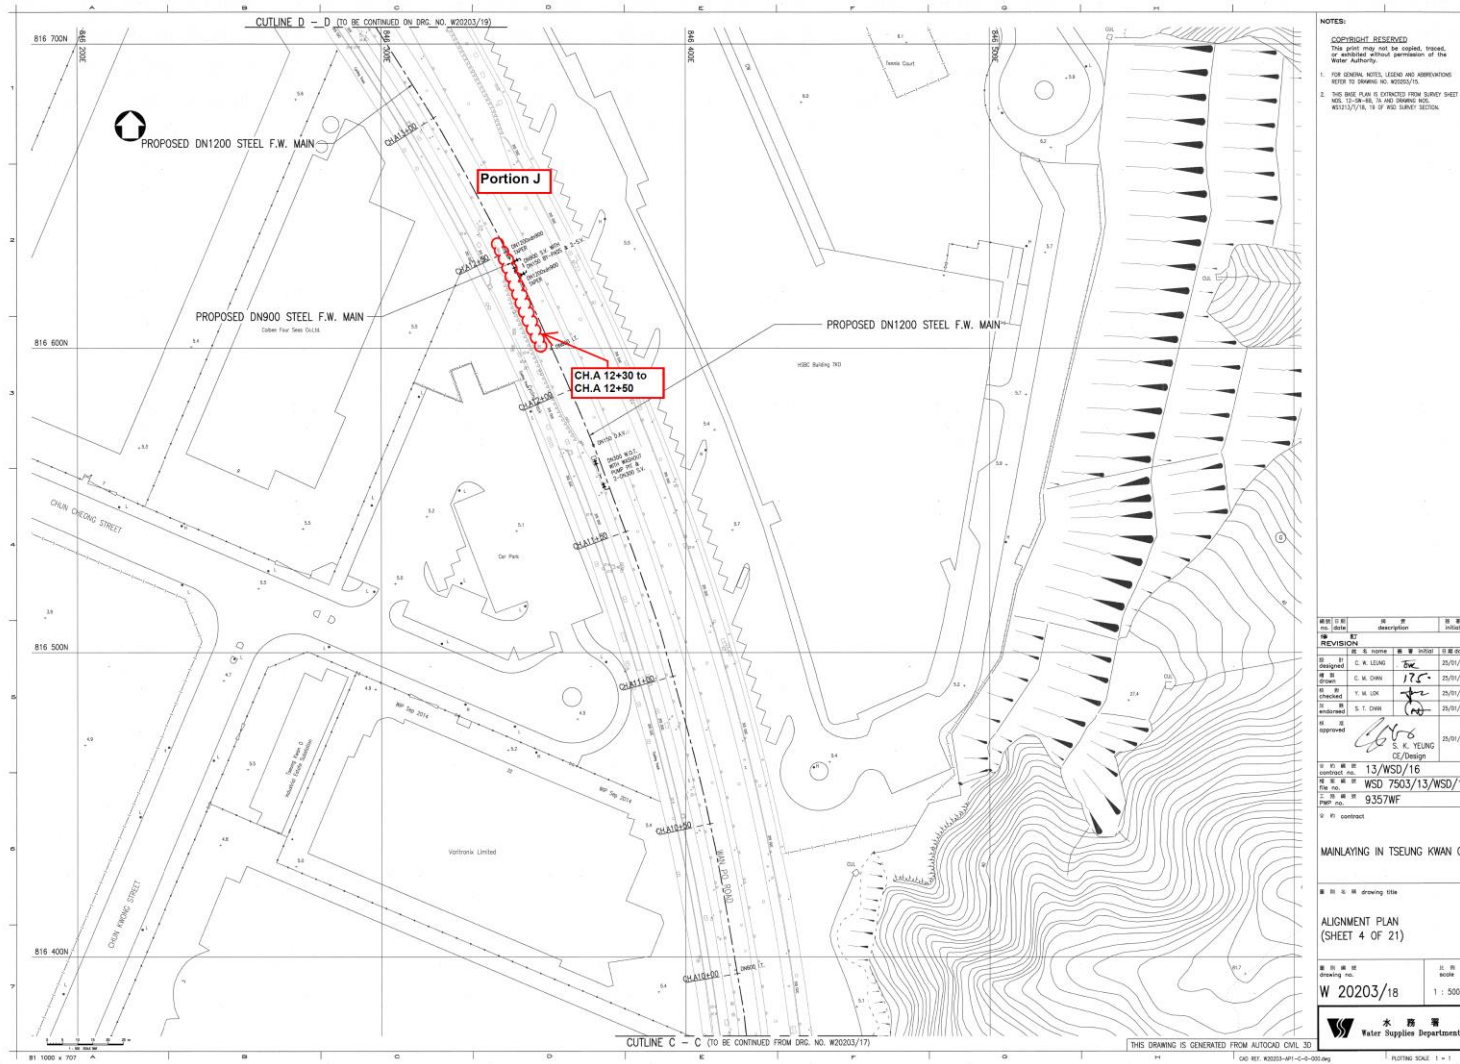

NOTES:

1. CONTRACT RESERVED. This plan may not be copied, traced, or amended without permission of the Water Authority.
2. FOR GENERAL NOTES, LEGEND AND ABBREVIATIONS REFER TO DRAWING NO. WSD203/16.
3. THIS BLUE PLAN IS EXTRACTED FROM SURVEY SHEET NO. 13-30-46, 13-40-30 AND 13-40-31, 13-40-32, 13-40-33, 13-40-34, 13-40-35, 13-40-36, 13-40-37, 13-40-38, 13-40-39, 13-40-40, 13-40-41, 13-40-42, 13-40-43, 13-40-44, 13-40-45, 13-40-46, 13-40-47, 13-40-48, 13-40-49, 13-40-50, 13-40-51, 13-40-52, 13-40-53, 13-40-54, 13-40-55, 13-40-56, 13-40-57, 13-40-58, 13-40-59, 13-40-60, 13-40-61, 13-40-62, 13-40-63, 13-40-64, 13-40-65, 13-40-66, 13-40-67, 13-40-68, 13-40-69, 13-40-70, 13-40-71, 13-40-72, 13-40-73, 13-40-74, 13-40-75, 13-40-76, 13-40-77, 13-40-78, 13-40-79, 13-40-80, 13-40-81, 13-40-82, 13-40-83, 13-40-84, 13-40-85, 13-40-86, 13-40-87, 13-40-88, 13-40-89, 13-40-90, 13-40-91, 13-40-92, 13-40-93, 13-40-94, 13-40-95, 13-40-96, 13-40-97, 13-40-98, 13-40-99, 13-40-100.

REVISED BY	DATE	DESCRIPTION	INITIAL
REVISION:			
1	25/01/17	DESIGNED	C. K. LING
2	25/01/17	CHECKED	T. M. LOK
3	25/01/17	APPROVED	S. T. CHAN
4	25/01/17	DESIGNED	S. K. YELING

CONTRACT NO. 13/WSD/16
 DRAWING NO. WSD 7503/13/WSD/16
 SHEET NO. 9357WF
 DRAWING TITLE: MAINLAYING IN TSEUNG KWAN O
 DRAWING NO.: W 20203/18
 SCALE: 1:500
 DEPARTMENT: Water Supplies Department

Figure B4. Location Plan for Portion J - CH.A 12+30 to CH.A 12+50

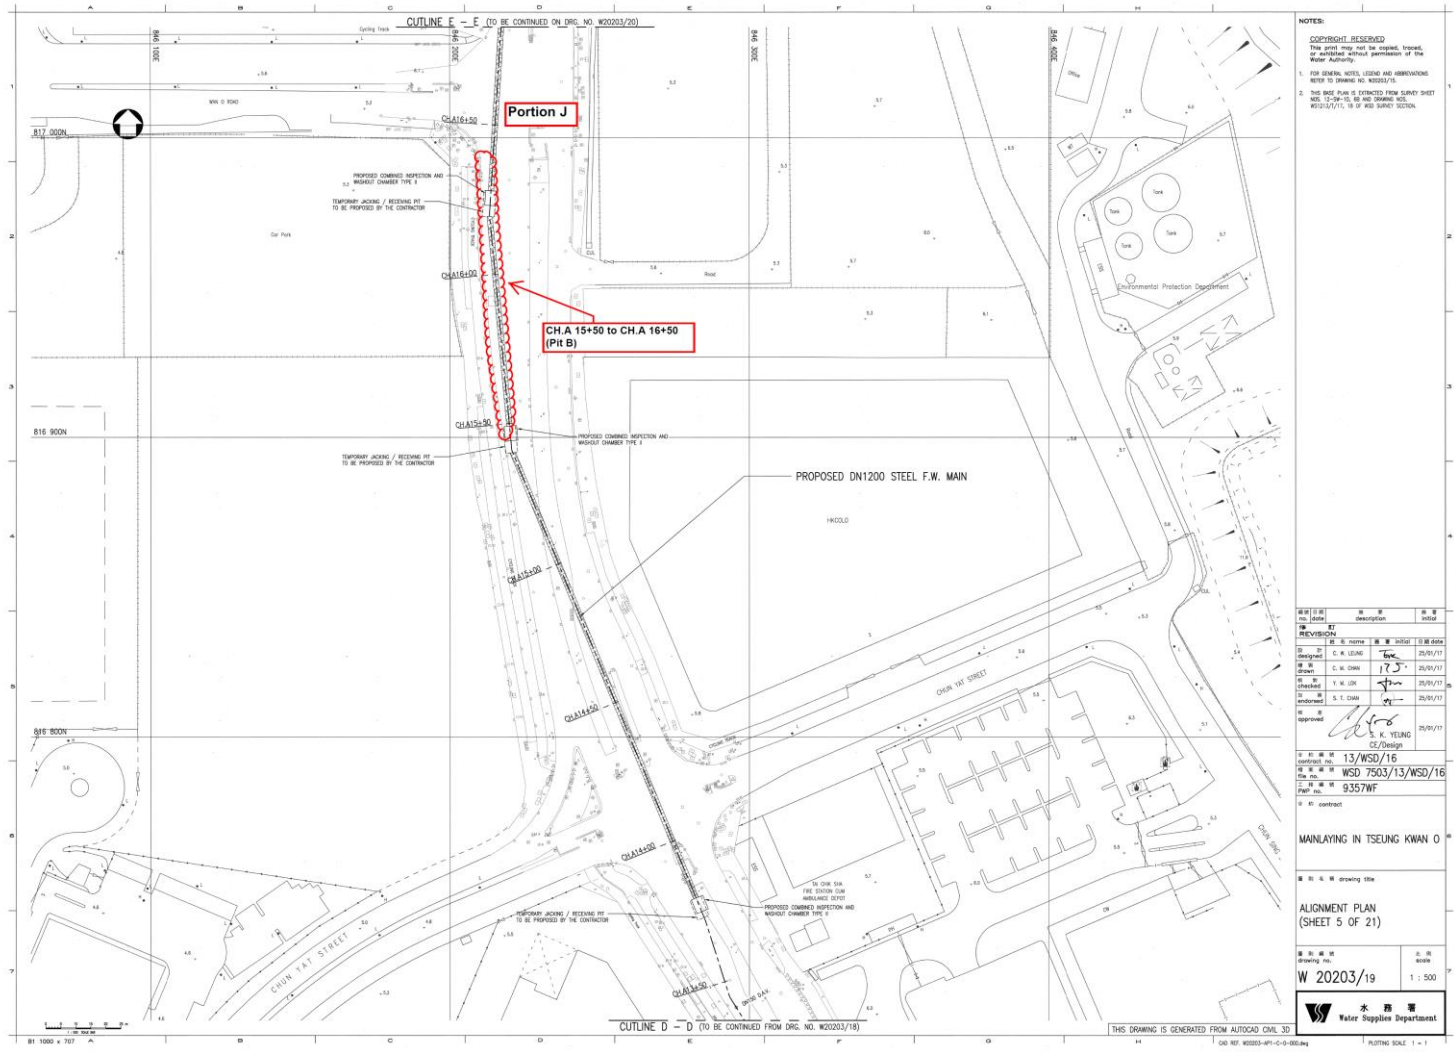


Figure B6. Location Plan for Portion J – CH. A15+50 to CH.A 16+50 (Pit B)

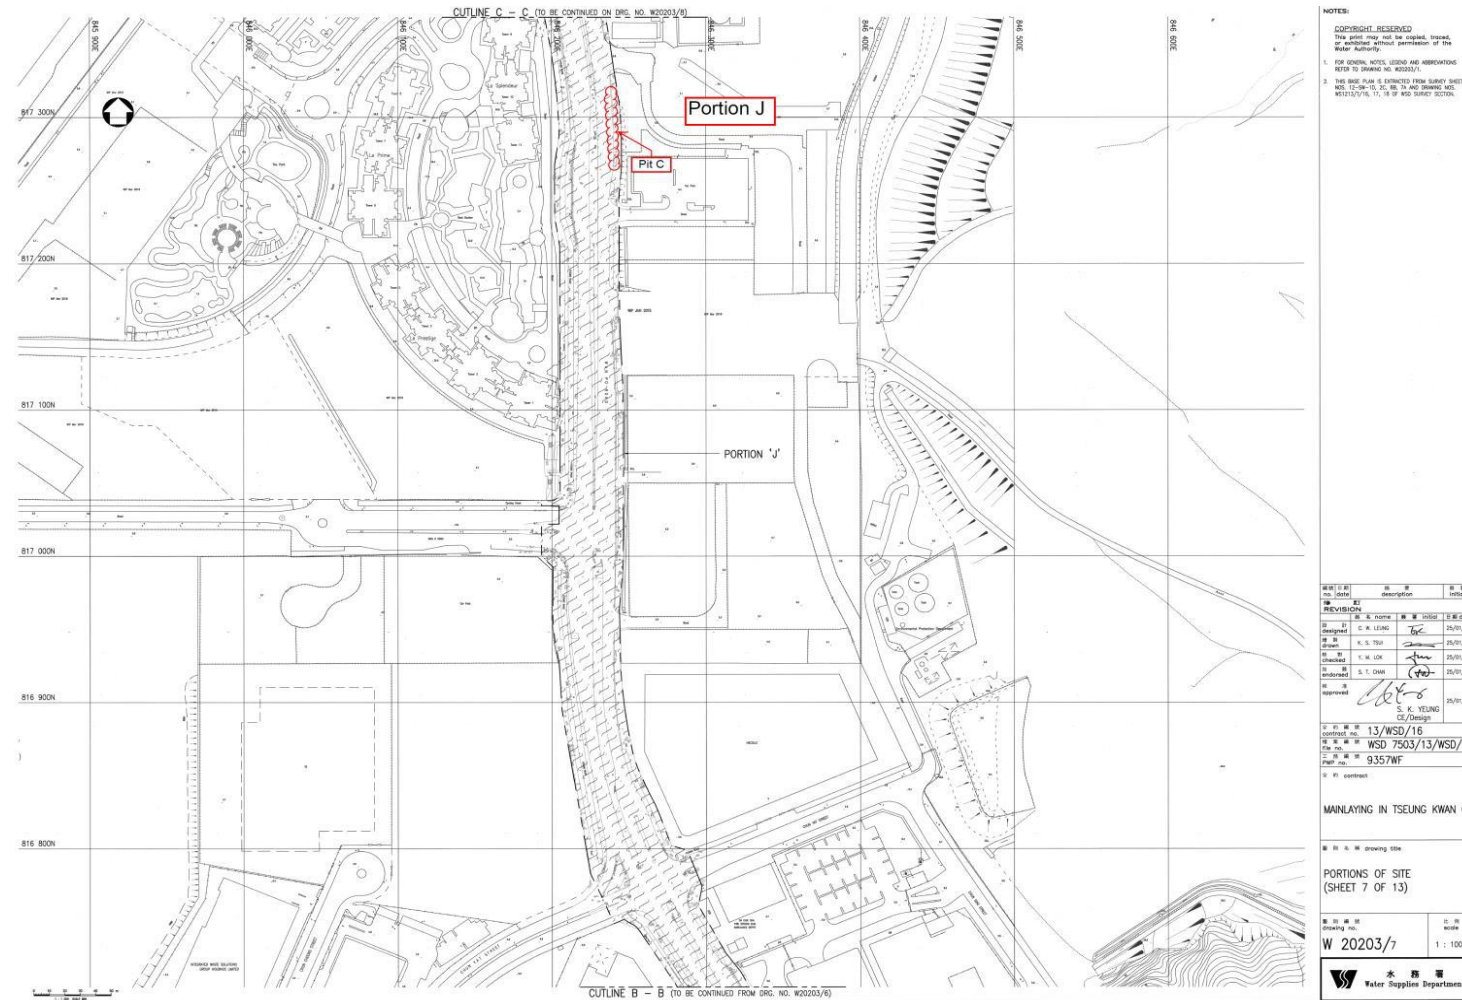


Figure B7. Location Plan for Portion J – CH.A 19+15 to CH.A 19+50 (Pit C)

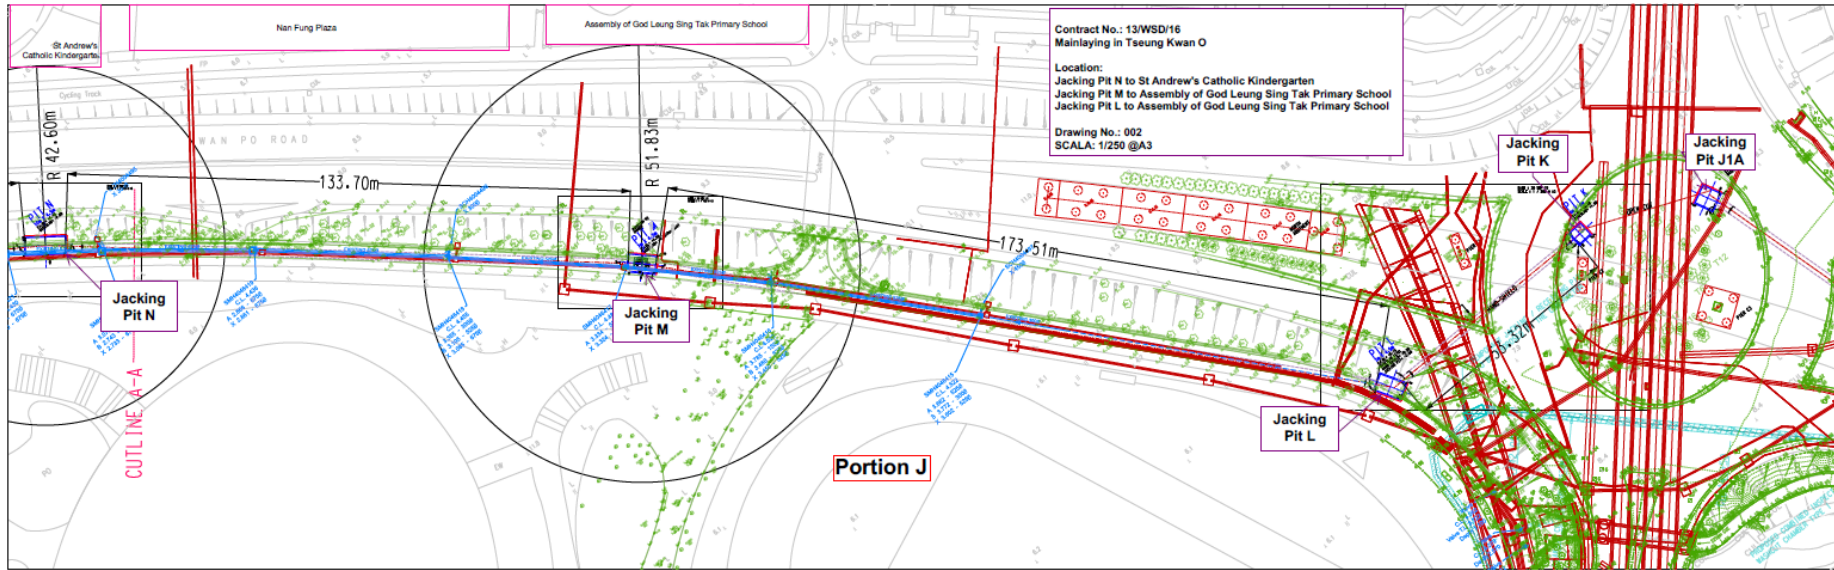


Figure B8a. Location Plan for Portion J – Pit L-M-N, K, J1A

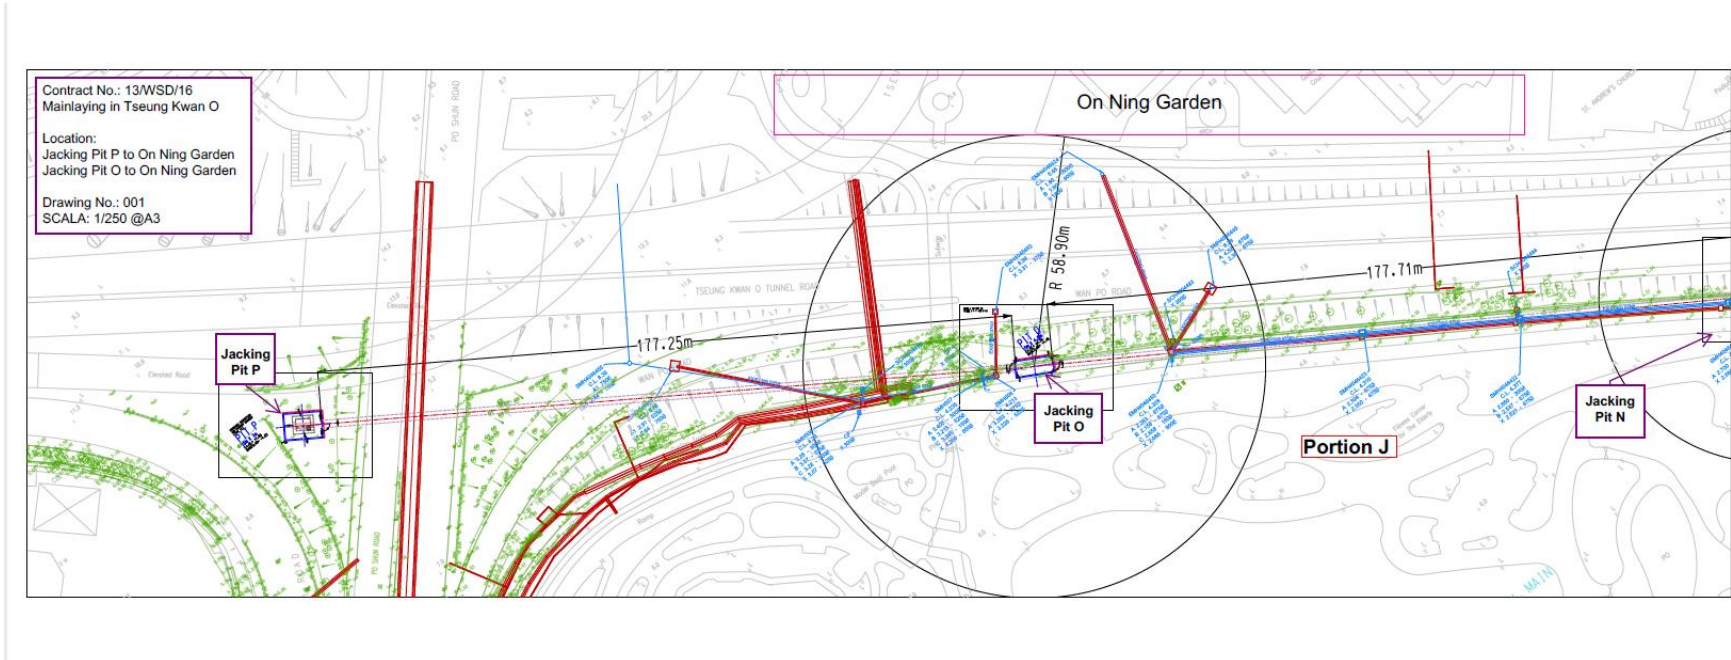


Figure B8b. Location Plan for Portion J – Pit N-O-P

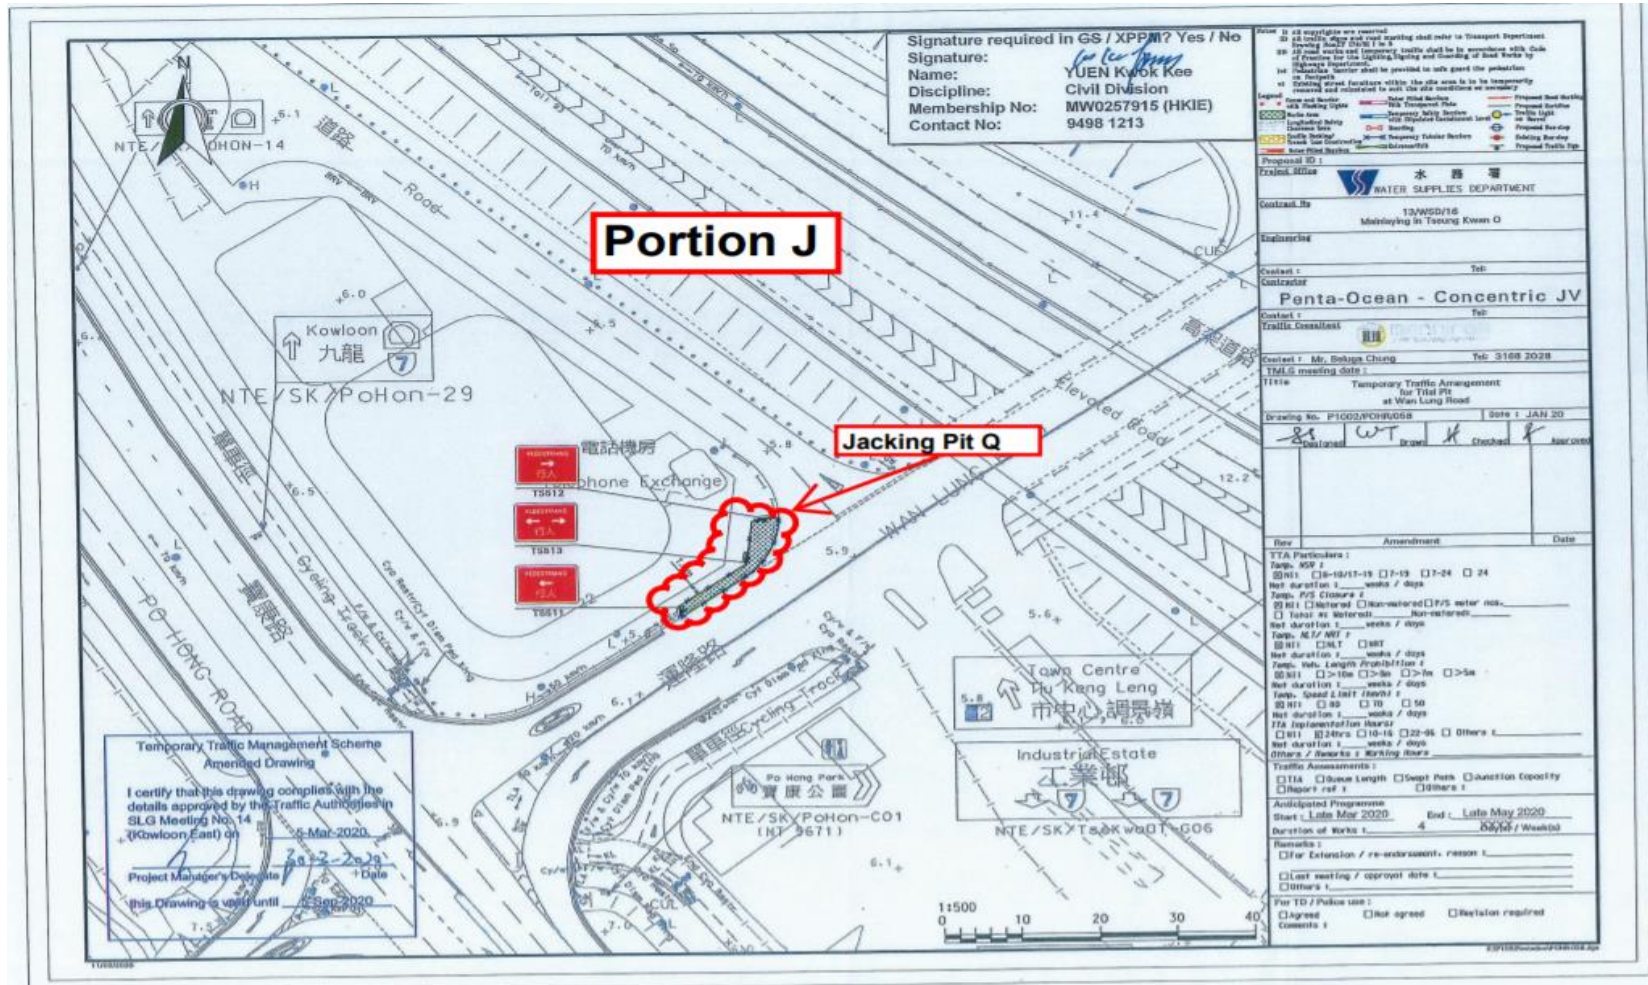


Figure B8c. Location Plan for Portion J – Pit Q

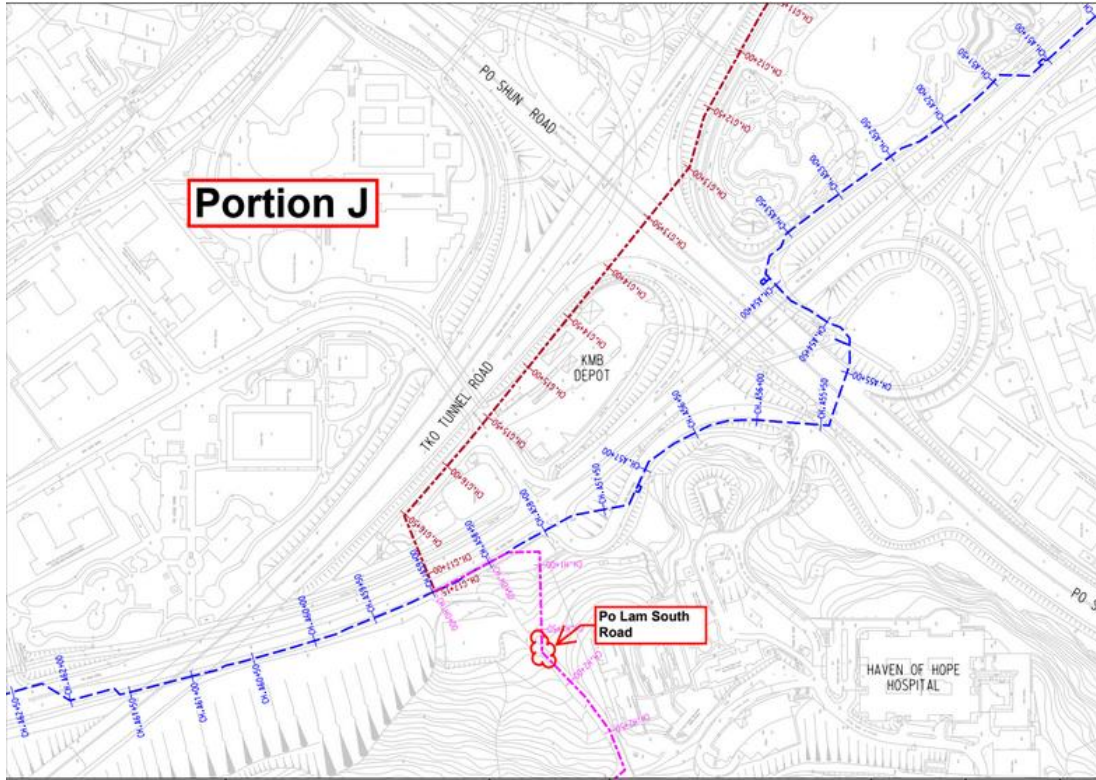


Figure B9a. Location Plan for Mau Wu Tsai 1

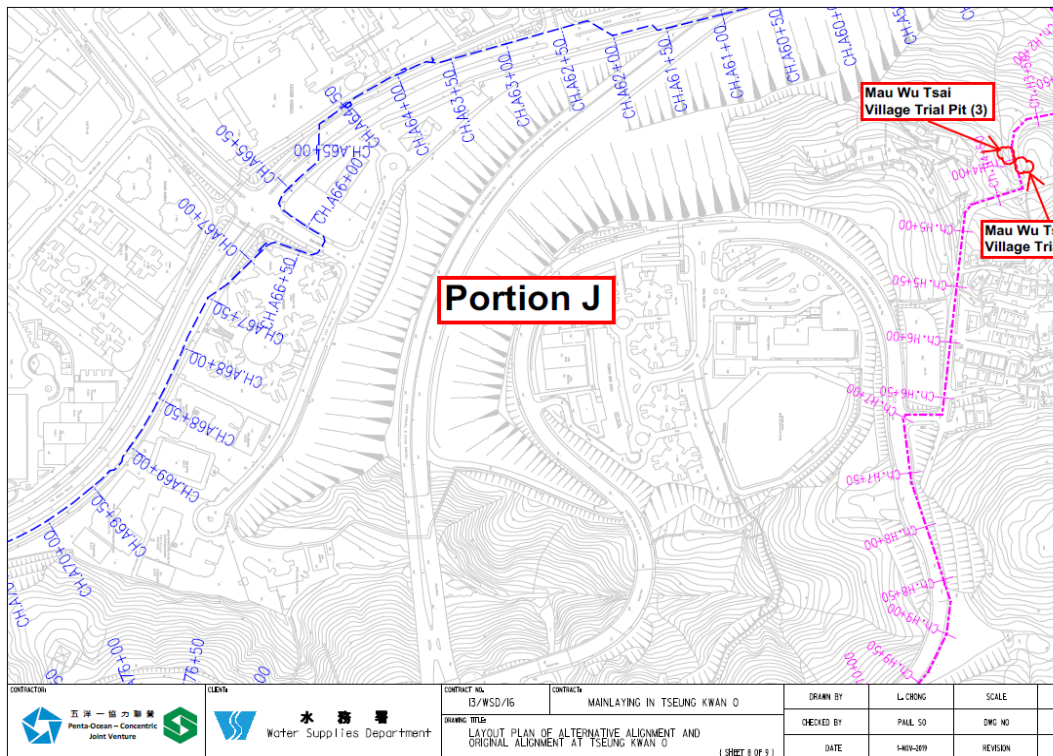


Figure B9b. Location Plan for Mau Wu Tsai 2 & 3

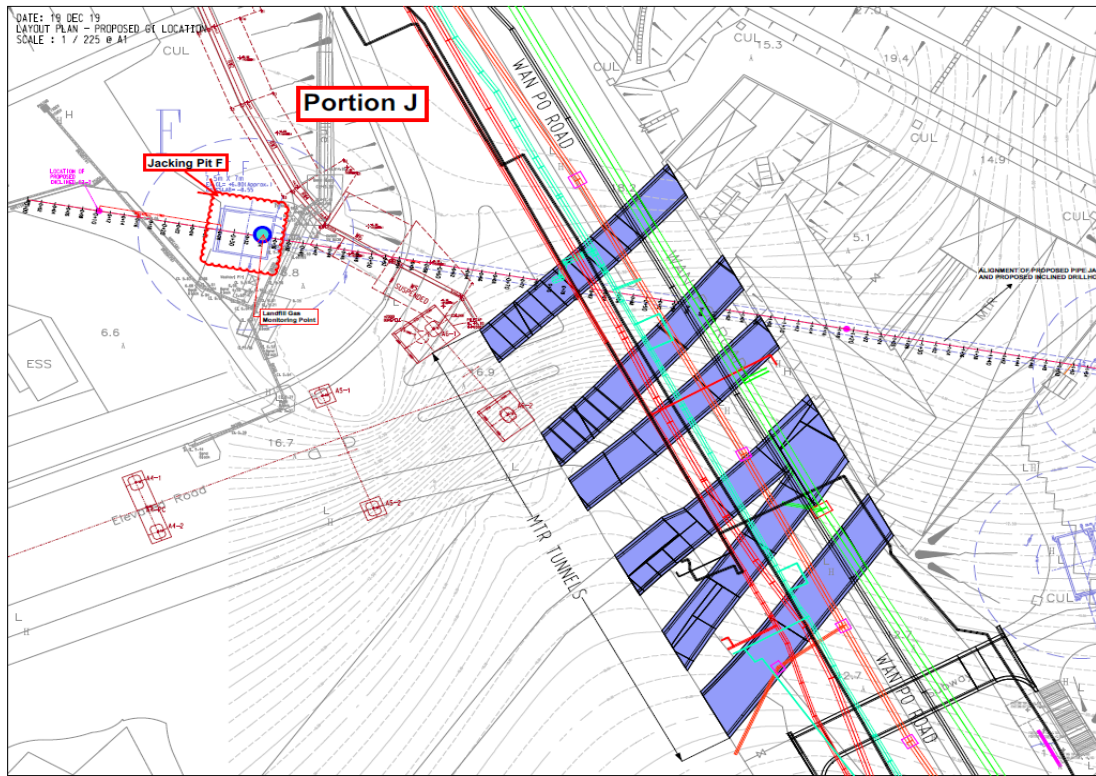


Figure B10. Location Plan for Jacking Pit F

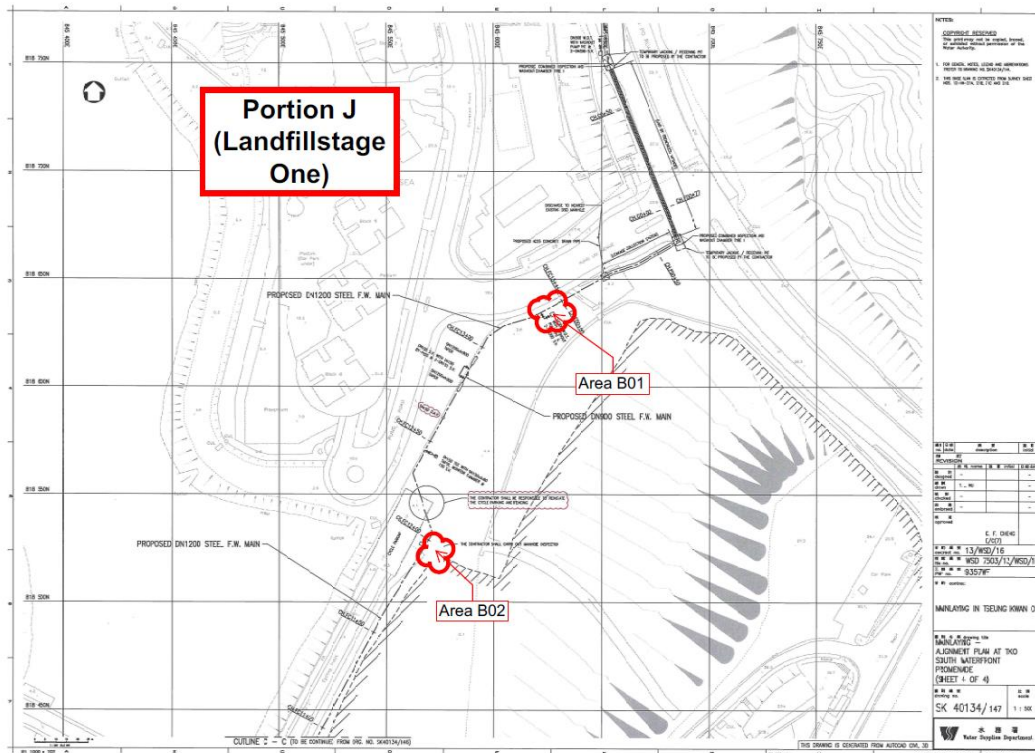


Figure B11a. Location Plan – Landfill Stage 1 (Area B01-B02)

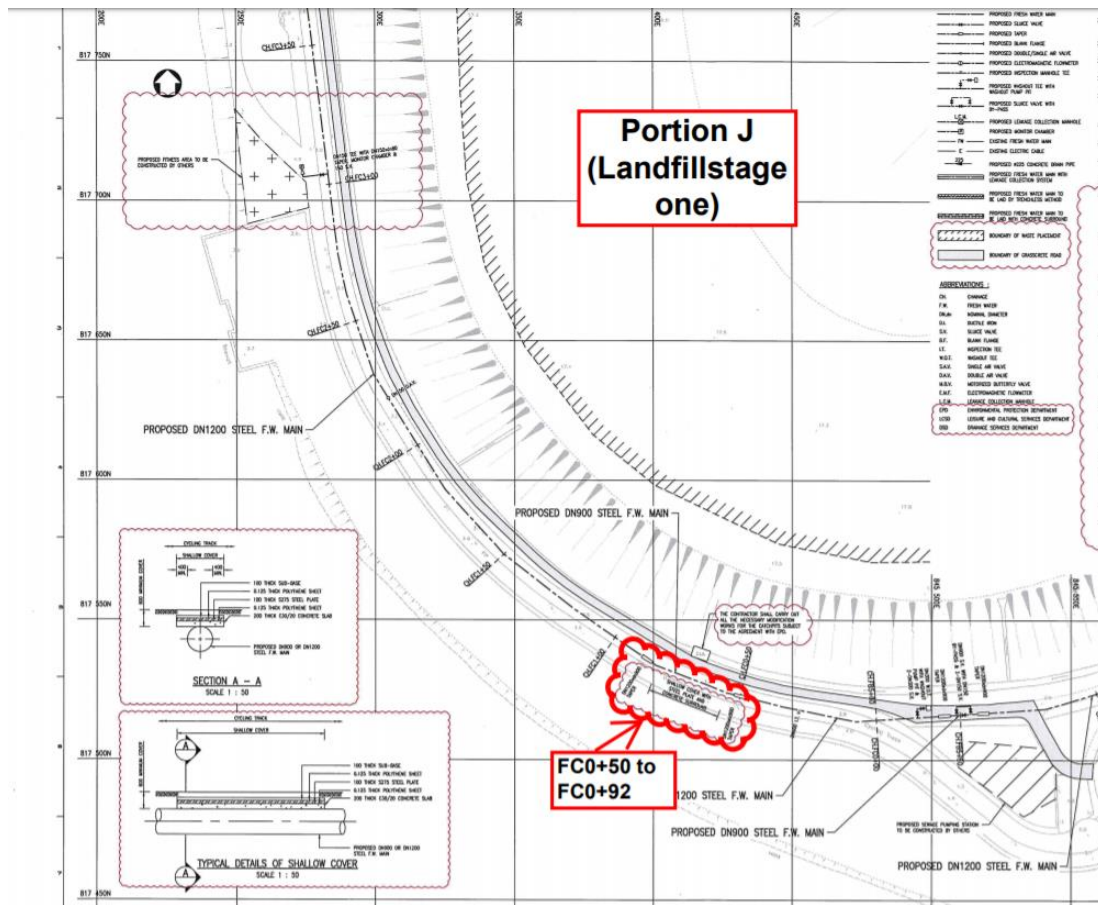


Figure B11b. Location Plan – Landfill Stage 1 (Area FC0+50 -FC0+92)

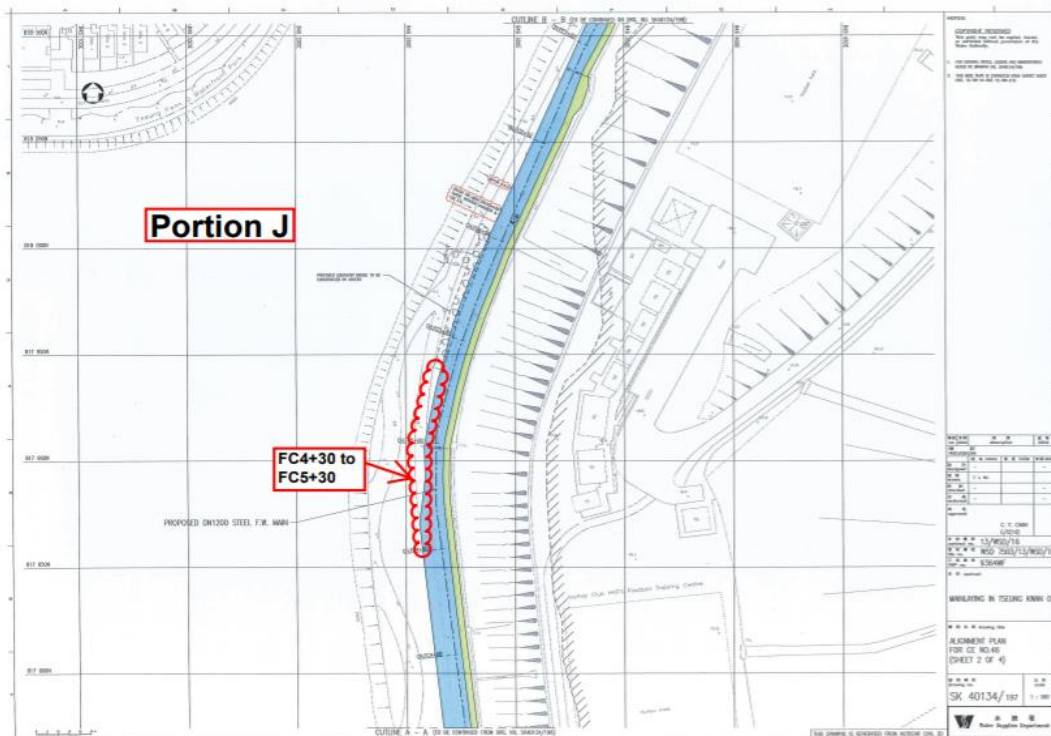


Figure B11c. Location Plan – Landfill Stage 1 (Area FC4+30 -FC5+30)

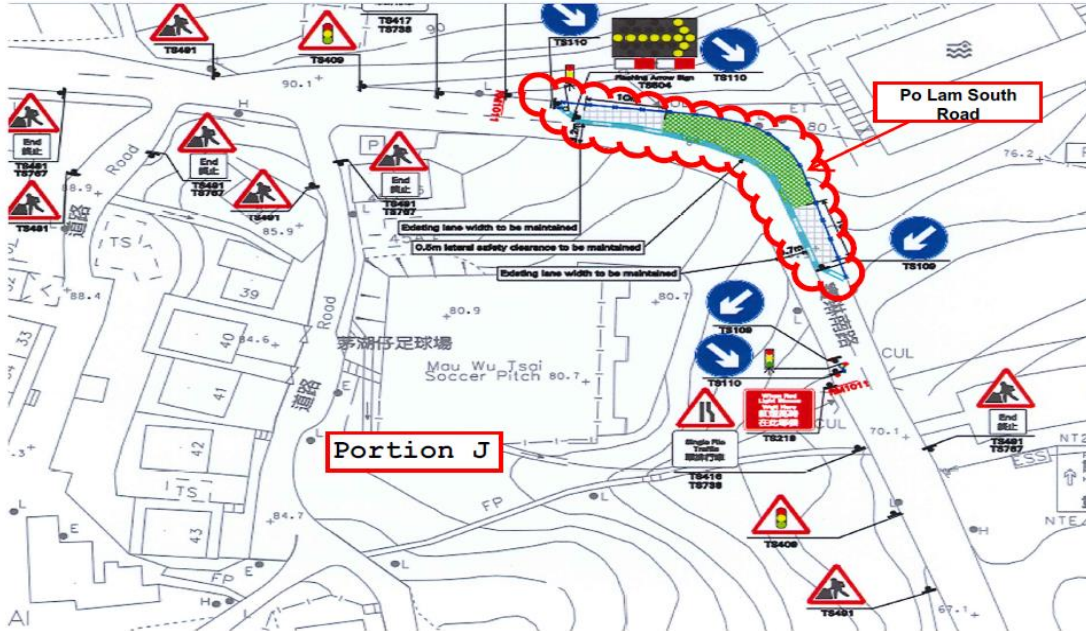


Figure B12. Monitoring Location – Po Lam South Road

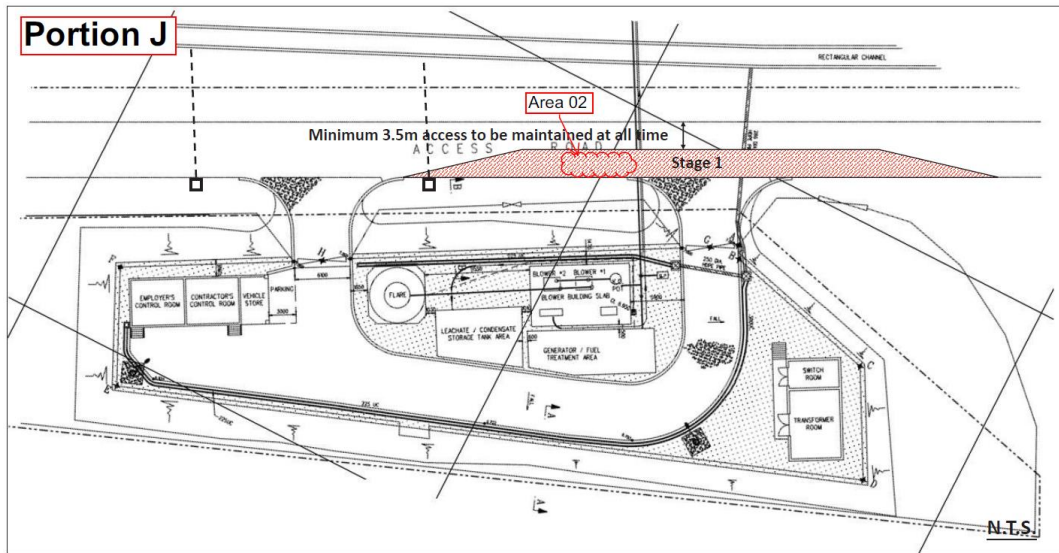


Figure B13. Monitoring Location – Area A02

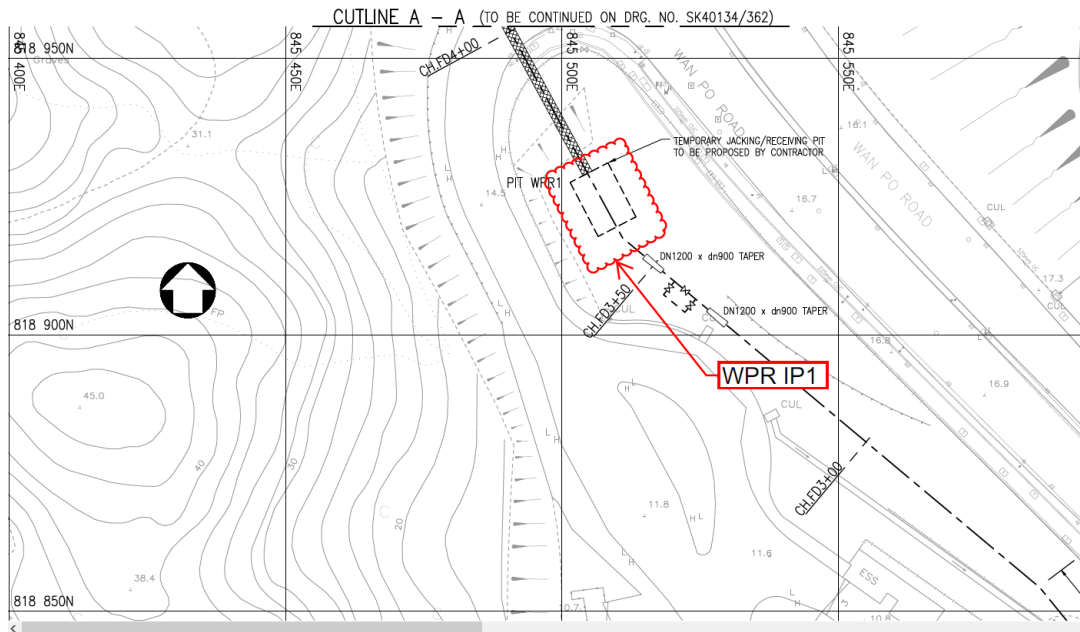


Figure B14. Location Plan for WPR IP1

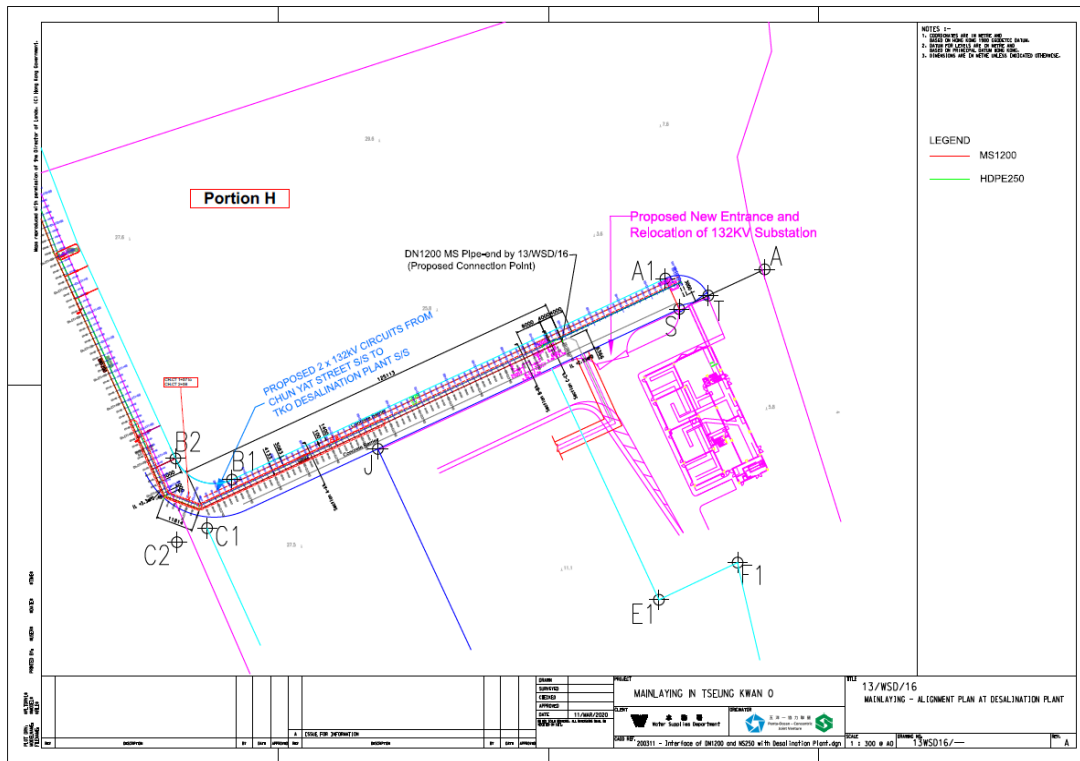


Figure B15a. Location Plan for CH.CT 0+07 - 2+58

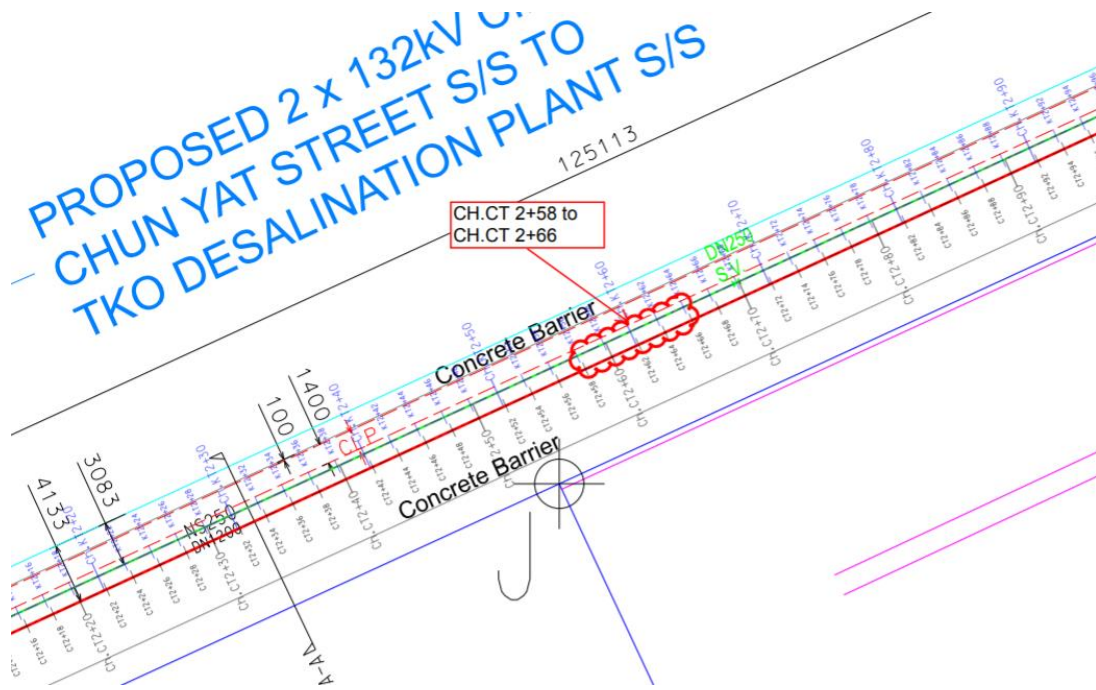


Figure B15b. Location Plan for CH.CT 2+58 – 2+66

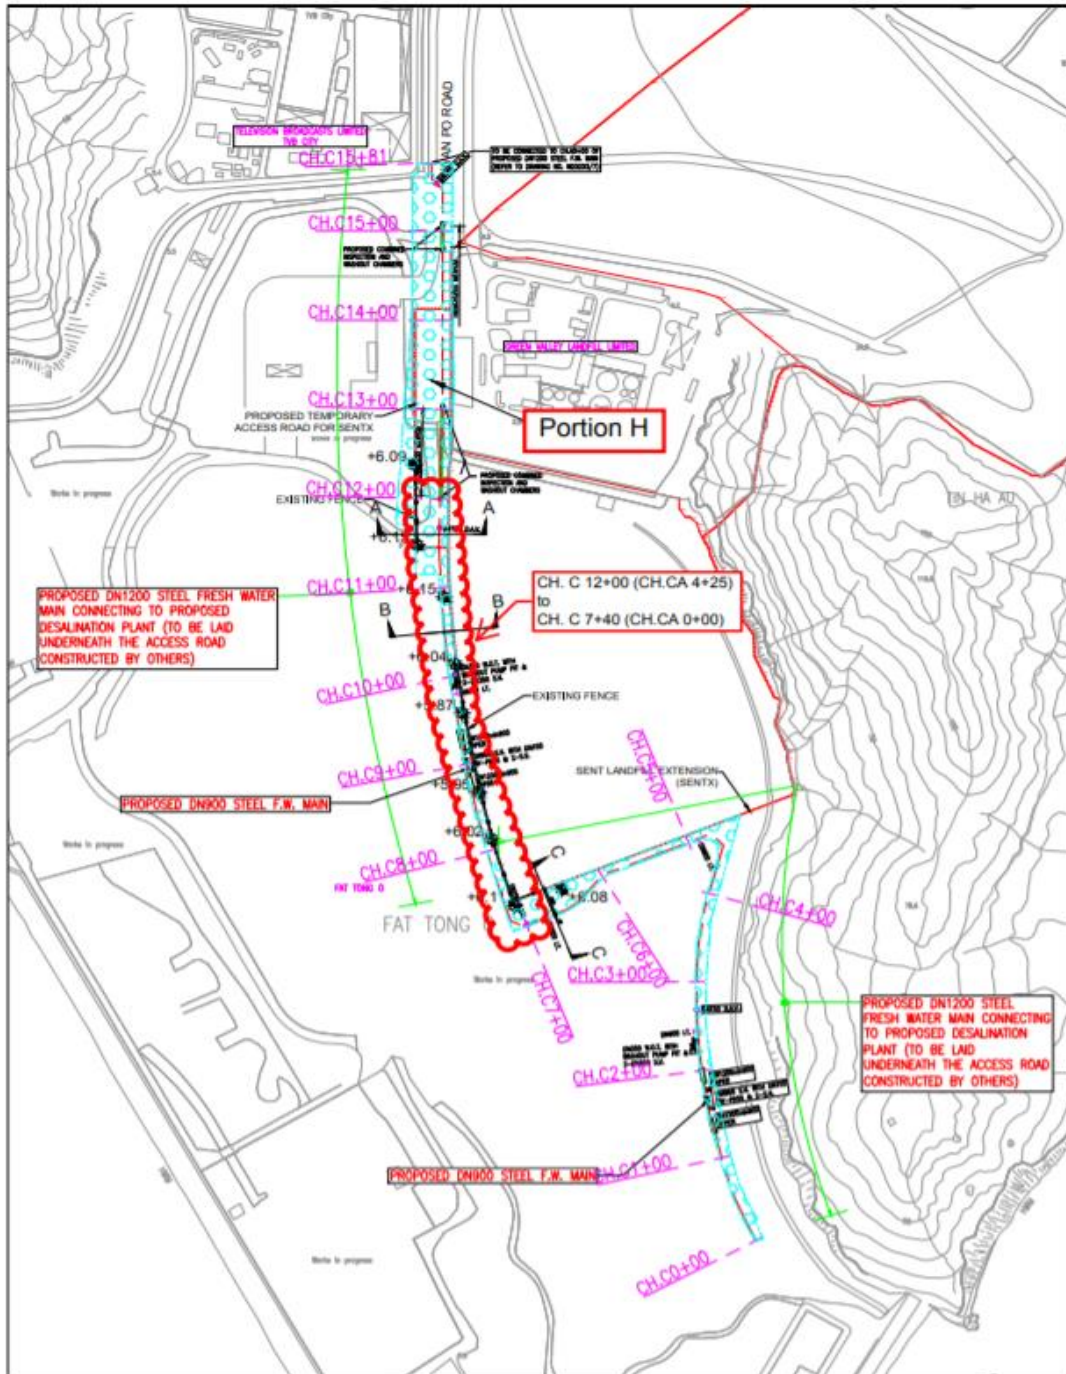


Figure B16. Location Plan for Portion H– CH.C 7+40~CH.C 12+00 (CH.CA 0+00 ~ CH.CA4+25)

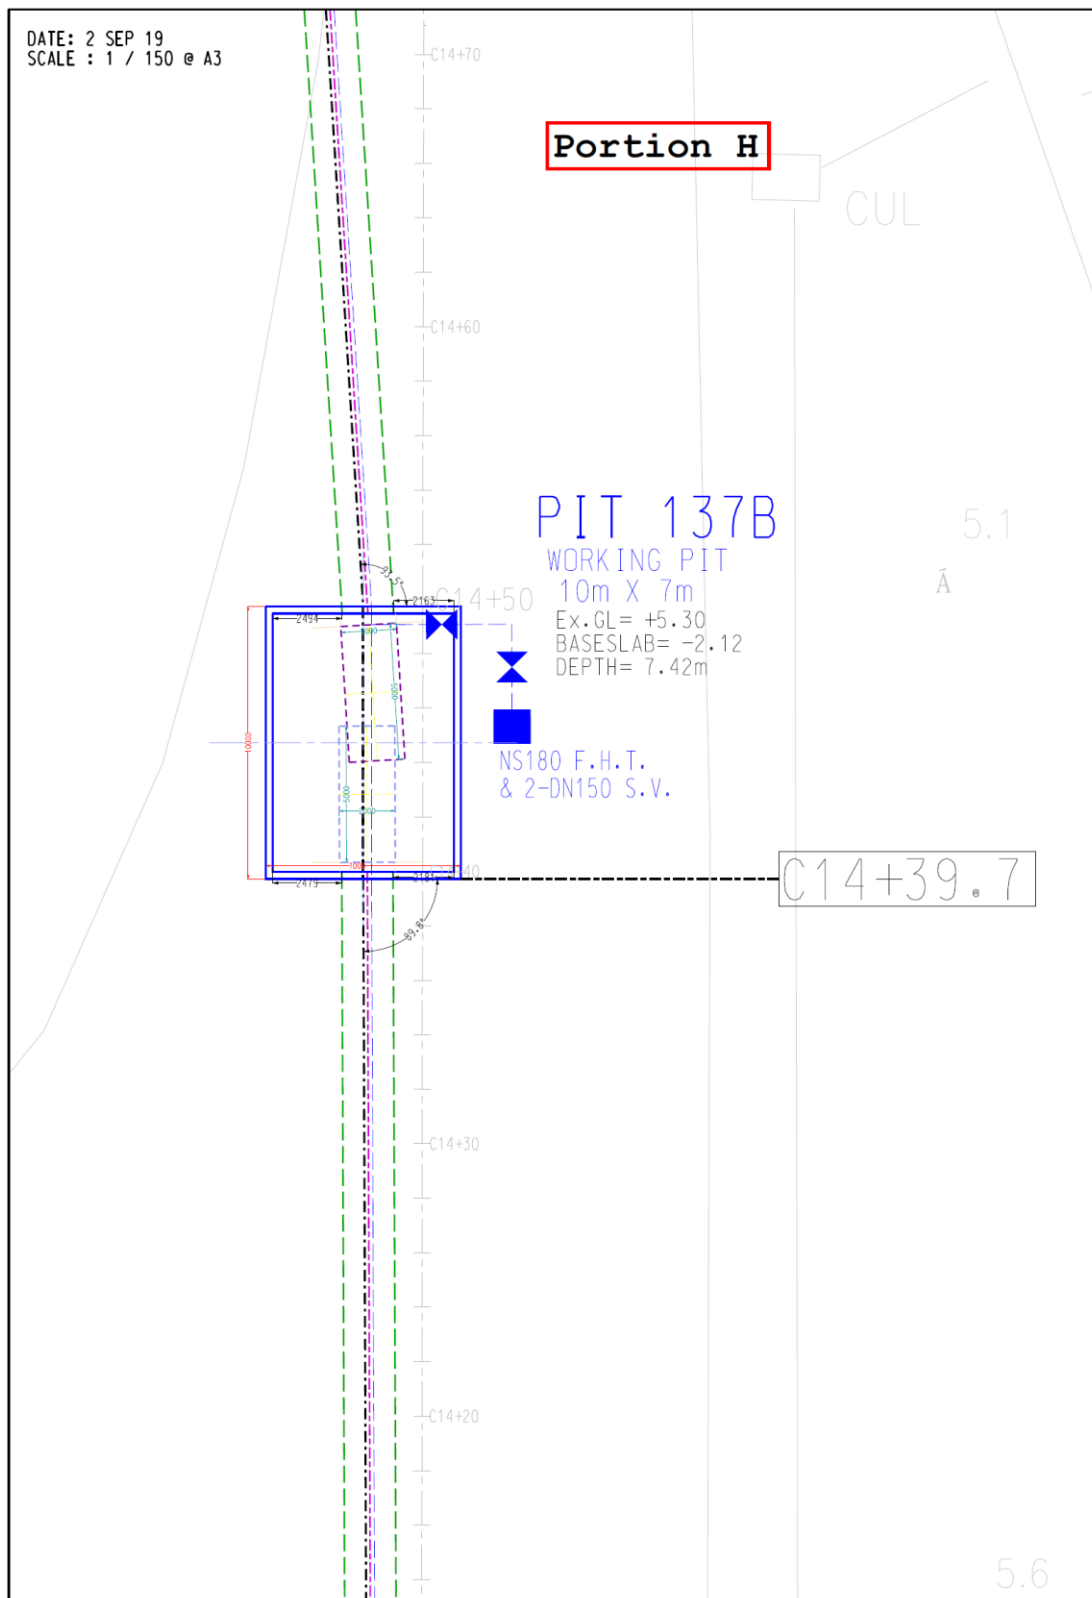


Figure B17a. Location Plan for Portion H- Pit 137B

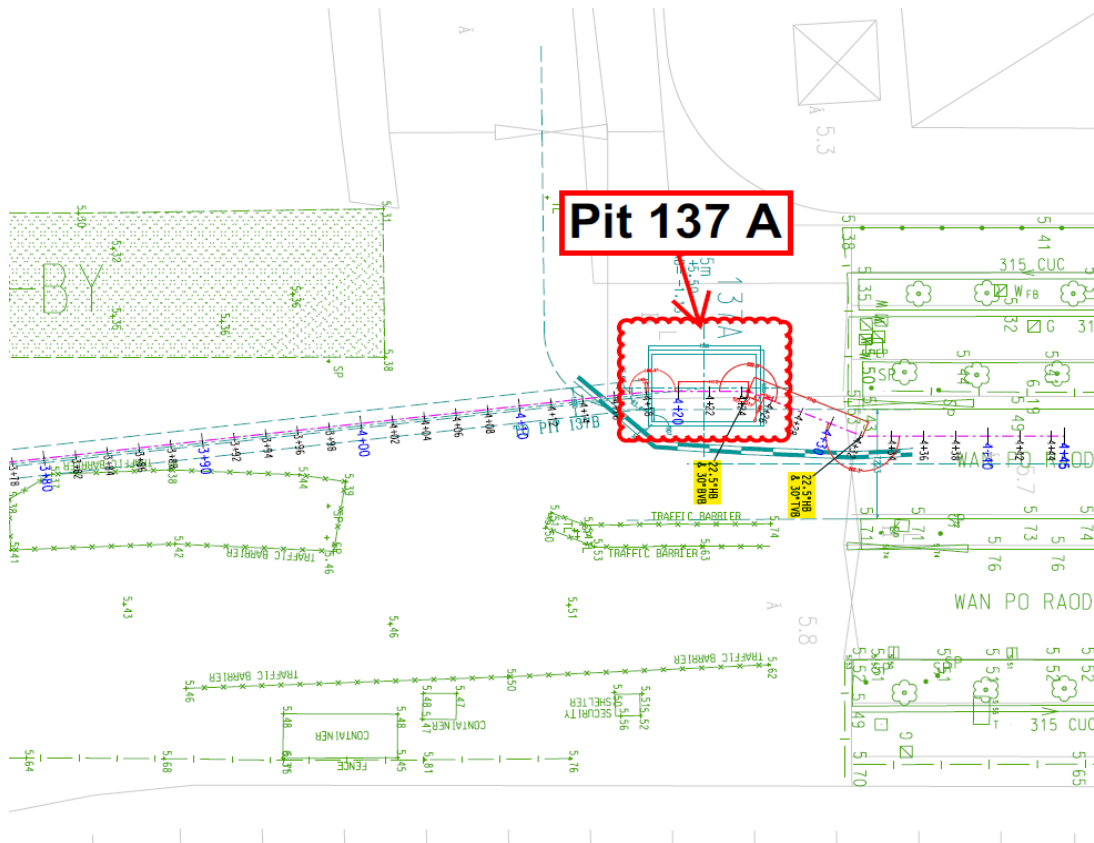


Figure B17b. Location Plan for Portion H- Pit 137A

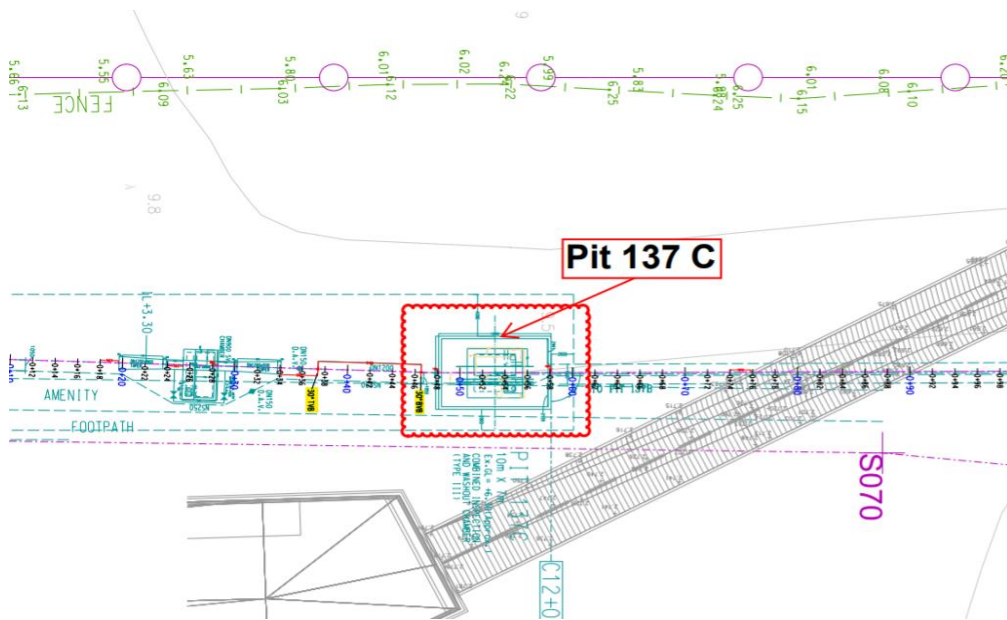


Figure B17c. Location Plan for Portion H- Pit 137C

Appendix C

Summary of Implementation Status of Environmental Mitigation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
Air Quality								
S4.8.1	Impervious dust screen or sheeting will be provided to enclose scaffolding from the ground floor level of building for construction of superstructure of the new buildings.	Land site/ During Construction	Contractor(s)		✓		N/A	Air Pollution Control (Construction Dust)
S4.8.1	Impervious sheet will be provided for skip hoist for material transport.	Land site/ During Construction, particularly dry season	Contractor(s)		✓		NA	
S4.8.1	The area where dusty work takes place should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after dusty activities as far as practicable.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	All dusty materials should be sprayed with water or a dust suppression chemical immediately prior to any loading, unloading or transfer operation.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	Dropping heights for excavated materials should be controlled to a practical height to minimize the fugitive dust arising from unloading.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	During transportation by truck, materials should not be loaded to a level higher than the side and tail boards, and should be dampened or covered before transport.	Land site/ During Construction	Contractor(s)		✓		N/A	
S4.8.1	Wheel washing device should be provided at the exits of the work sites. Immediately before leaving a construction site, every vehicle shall be washed to remove any dusty material from its body and wheels as far as practicable.	Land site/ During Construction	Contractor(s)		✓		N/A	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S4.8.1	Road sections between vehicle-wash areas and vehicular entrance will be paved.	Land site/ During Construction	Contractor(s)		✓		N/A	
S4.8.1	Hoarding of not less than 2.4m high from ground level will be provided along the length of the Project Site boundary.	Land site/ During construction	Contractor(s)	✓	✓		N/A	
S4.8.1	Haul roads will be kept clear of dusty materials and will be sprayed with water so as to maintain the entire road surface wet at all times.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.8.1	Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets or sprayed with water to maintain the entire surface wet all the time.	Land site/ During construction	Contractor(s)		✓		Implemented, rectified after observation	
S4.8.1	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Land site/ During construction	Contractor(s)		✓		N/A	
S4.8.1	All exposed areas will be kept wet always to minimise dust emission.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.8.1	Ultra-low-sulphur diesel (ULSD) will be used for all construction plant on-site, as defined as diesel fuel containing not more than 0.005% sulphur by weight) as stipulated in Environment, Transport and Works Bureau Technical Circular (ETWB-TC(W)) No 19/2005 on Environmental Management on Construction Sites.	Land site/ During construction/ During Operation	Contractor(s)		✓	✓	Implemented	Environment, Transport and Works Bureau Technical Circular (ETWB-TC(W)) No 19/2005 on Environmental Management on Construction Sites

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S4.8.1	The engine of the construction equipment during idling will be switched off.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.8.1	Concrete batching plant will be required on site. control measures recommended in the Guidance Note on a Best Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be implemented. The control measures recommended in the Guidance Note on a Best Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be	Land site/ During construction	Contractor(s)		✓		N/A	Guidance Note on a Best
S4.8.1	Regular maintenance of construction equipment deployed on-site will be conducted to prevent black smoke emission.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.10	To ensure proper implementation of the recommended dust mitigation measures and good construction site practices during the construction phase, environmental site audits on weekly basis is recommended throughout the construction period.	Land site/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
Noise								
S5.7	Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase.	All area/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Mobile plant, if any, will be sited as far away from NSRs as possible.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Plants known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Use of Quiet Powered Mechanical Equipment (QPME).	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Movable noise barriers of 3m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
	than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps.							
S5.7	The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Construction activities (e.g. excavation/shoring, reinstatement (asphalt), and pipe jacking) will be planned and carried out in sequence, such that items of PME proposed for these activities will not be operated simultaneously.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works
S5.7	PMEs will not be used at the works areas near educational institutions with residual impact (ie the "influence area" within a radius of 40m) during school hours in order to reduce impact to the educational institutions.	Noise control / During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works
S5.7	Noise enclosures or acoustic sheds would be used to cover stationary PME such as generators. Portable/Movable noise enclosure made of material with superficial surface density of at least 7 kg m ⁻² may be used for screening the noise from operation of the saw/groover, concrete.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		N/A	
S5.9	Sawcutting pavement, breaking up of pavement, excavation /shoring, pipe laying, backfilling, reinstatement (concrete) and pipe jacking shall be scheduled outside the examination period.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		Implemented	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S5.9	In view the duration of noise exceedance at Creative Secondary School, PLK Laws Foundation College, TKO Kei Tak Primary School and School of Continuing and Professional Studies-CUHK is limited to 8 weeks, the construction work in the influence areas near the four schools shall be scheduled during long school holidays (eg summer holiday, Easter holiday or Christmas holiday, etc) as far as practicable. Scheduling the construction work for the four schools.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		Implemented	
S5.10	A noise monitoring programme shall be implemented for the construction phase.	Designated monitoring stations as defined in EM&A Manual/During construction phase	Environmental Team (ET)		✓		Implemented	
S5.10	The effectiveness of on-site control measures could also be evaluated through the regular site audits.	All facilities/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
Water Quality								
S6.9	Dredged marine sediment will be disposed of in a gazetted marine disposal area in accordance with marine dumping permit conditions of the Dumping at Sea Ordinance (DASO).	Marine Dredging/ During construction	Contractor(s)		✓		N/A	Dumping at Sea Ordinance (DASO)
S6.9	Disposal vessels will be fitted with tight bottom seals in order to prevent leakage of material during transport.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	Barges will be filled to a level, which ensures that material does not spill over during transport to the disposal site and that adequate freeboard is maintained to ensure that the decks are not washed by wave action.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	After dredging, any excess materials will be cleaned from decks and exposed fittings before the vessel is moved from the dredging area.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	All vessels should be well maintained and inspected before use to limit any potential discharges to the marine environment.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	All vessels must have a clean ballast system.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	No discharge of sewage/grey wastewater should be allowed. Waste water from potentially contaminated area on working vessels should be minimized and collected. These kinds of wastewater should be brought back to port and discharged at appropriate collection and treatment system.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	No soil waste is allowed to be disposed overboard.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementati on Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.9	Silt removal facilities such as silt traps or sedimentation facilities will be provided to remove silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities will be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented, rectified after observation	ProPECC PN 1/94 TM Standard under the WPCO
S6.9	Earthworks to form the final surfaces will be followed up with surface protection and drainage works to prevent erosion caused by rainstorms.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9	Appropriate surface drainage will be designed and provided where necessary.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-
S6.9	The precautions to be taken at any time of year when rainstorms are likely together with the actions to be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	ProPECC PN 1/94
S6.9	Oil interceptors will be provided in the drainage system where necessary and regularly emptied to prevent the release of oil and grease into the storm water drainage system after accidental spillages.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented, rectified after observation0	-
S6.9	Temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge, if any, will be adequately designed for the controlled release of storm flows.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.9	The temporary diverted drainage, if any, will be reinstated to the original condition when the construction work has finished or when the temporary diversion is no longer required.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-
S6.9	Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the construction workers over the construction site to prevent direct disposal of sewage into the water environment.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9 and S6.12	The sterilization water should be dechlorinated with total residual chlorine (TRC) level below 1 mg/L before discharge to public sewer. In situ testing of TRC should also be conducted for the discharge of chlorinated water for pipeline disinfection to ensure sufficient dechlorination before discharge to public sewer.	Sterilization of water mains prior to commissioning	Contractor(s)		✓	✓	N/A	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	The cleaning and flushing water should also be treated and desilted to the relevant discharge requirement stipulated in TM-DSS before discharging.	Sterilization of water mains prior to commissioning	Contractor(s)		✓	✓	N/A	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	Site drainage should be well maintained and good construction practices should be observed to ensure that oil, fuels, solvents and other chemicals are managed, stored and handled properly and do not enter the nearby water streams.	Land site & drainage/ During construction/ During operation	Contractor(s)		✓	✓	Implemented, rectified after observation	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.12	Regular site inspections will be carried out in order to confirm that regulatory requirements are being met and that contractors are implementing the standard site practice and mitigation measures as proposed to reduce potential impacts to water quality.	During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
Waste Management								
S8.5	Nomination of approved personnel to be responsible for standard site practices, arrangements for collection and effective disposal to an appropriate facility of all wastes generated at the site.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Training of site personnel in proper waste management and chemical handling procedures. Training will be provided to workers on the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling at the beginning of the construction works.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Provision of sufficient waste disposal points and regular collection for disposal.	All area/ During construction/ During operation	Contractor(s)		✓	✓	Implemented	DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	Appropriate measures to reduce windblown litter and dust transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	All area/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	A waste management plan (WMP) as stated in the "ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites" for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established and implemented during the construction phase as part of the Environmental Management Plan (EMP). The Contractor will be required to prepare the EMP and submits it to the Architect/ Engineer under the Contract for approval prior to implementation.	All area/ During construction	Contractor(s)		✓		Implemented	ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites
S8.5	Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Centre at Tsing Yi.	All area/ During construction	Contractor(s)		✓		N/A	Chapters 2 & 3 Code of Practice on the Packaging Labelling & Storage of

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
								Chemical Wastes published under the Waste Disposal Ordinance (Cap 354), Section 35
S8.5	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.	Land site/ During construction	Contractor(s)		✓		Implemented, rectified after observation	Waste Disposal Ordinance (Cap 354)
S8.5	A recording system for the amount of wastes generated/ recycled and disposal sites. The trip- ticket system will be included as one of the contractual requirements and implemented by the contractor(s).	Land site/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of material and their proper disposal.	Land site/ During construction/ During operation	Contractor(s)		✓		Implemented	WBTC 32/92, The Use of Tropical Hard Wood on Construction Site
S8.5	Encourage collection of aluminium cans and waste paper by individual collectors during construction with separate labelled bins provided to segregate these wastes from other general refuse by the workforce.	Land site/ During construction	Contractor(s)		✓		Implemented	ETWB TCW No. 33/2002, Management of Construction and Demolition Material Including Rock
S8.5	Any unused chemicals and those with remaining functional capacity will be recycled as far as possible.	Land site/ During construction	Contractor(s)		✓		N/A	-
S8.5	Use of reusable non-timber formwork to reduce the amount of C&D materials.	All areas/ During construction	Contractor(s)		✓		N/A	WBTC 32/92, The Use of Tropical Hard Wood on Construction Site
S8.5	Prior to disposal of construction waste, wood, steel and other metals will be separated to the extent practical, for re-use and/or recycling to reduce the quantity of waste to be disposed of to landfill.	All areas/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Proper storage and site practices to reduce the potential for damage or contamination of construction materials.	All areas/ During construction	Contractor(s)		✓		Implemented, rectified after observation	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	Plan and stock construction materials carefully to reduce amount of waste generated and avoid unnecessary generation of waste.	All areas/ During construction	Contractor(s)		✓		Implemented	-
S8.5	A Sediment Quality Report (SQR) for sampling and chemical testing of the sediment will be prepared and submitted to the EPD for approval. The approved detailed sampling and chemical testing will be carried out prior to the commencement of the dredging activities to confirm the sediment disposal method.	Marine works/ During construction	Contractor(s)		✓		N/A	ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The management of dredged/ excavated sediment management requirement from <i>ETWB TC(W) No. 34/2002</i> will be incorporated in the Specification of the Contract Documents.	Marine works/ During construction	WSD/ Contractor(s)		✓		Implemented	ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The contractor will open a billing account with EPD in accordance with the Waste Disposal (Charges for Disposal of Construction Waste) Regulation for the payment of disposal charges.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	Cap 354N Waste Disposal (Charges for Disposal of Construction Waste) Regulation
S8.5	A trip-ticket system will be established in accordance with DEVB TC(W) No. 6/2010 to monitor the reuse of surplus excavated materials off-site and disposal of construction waste and general refuse at transfer facilities/ landfills, and to control fly-tipping.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	The project proponent will also conduct regular inspection of the waste management measures implemented on site as described in the Waste Management Plan.	All area/ During construction	Contractor(s) / Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	A recording system (similar to summary table as shown in Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005) for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established during the construction phase.	All area/ During construction	Contractor(s)		✓		Implemented	Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005
S8.5	Inert C&D materials (public fill) will be reused within the Project as far as practicable.	All area/ During construction	Contractor(s)		✓		N/A	-
S8.5	Public fill and construction waste shall be segregated and stored in different containers or skips to facilitate reuse or recycling of materials and their proper disposal.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	To reduce the potential dust and water quality impacts of site formation works, C&D materials will be wetted as quickly as possible to the extent practice after filling.	All area/ During construction	Contractor(s)		✓		Implemented	Air Pollution Control (Construction Dust) Regulation (Cap 311R); WPCO (Cap 358)
S8.5	Open stockpiles of excavated/ fill materials or construction wastes on-site should be covered with tarpaulin or similar fabric.	Land site/ During Construction, particularly dry season	Contractor(s)		✓		Implemented	Air Pollution Control (Construction Dust) Regulation (Cap 311R)
S8.5	Chemical waste container shall be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Chemical waste container shall have a capacity of less than 450 L unless the specifications have been approved by the EPD.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	A label in English and Chinese shall be displayed on the chemical container in accordance with instructions prescribed in Schedule 2 of the Regulations.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be enclosed on at least 3 sides.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall have adequate ventilation.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary).	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be	All area/ During	Contractor(s)/		✓	✓	Implemented	Waste Disposal

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	arranged so that incompatible materials are appropriately separated.	construction/ During operation	WSD					(Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	General refuse will be stored in enclosed bins or compaction units separately from construction and chemical wastes.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Adequate number of waste containers will be provided to avoid over-spillage of waste.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	DEVB TC(W) No. 8/2010 Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	A reputable waste collector will be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimise odour, pest and litter impacts.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	N/A	-
S8.5	Recycling bins will be provided at strategic locations within the Site to facilitate recovery of recyclable materials (including aluminium can, waste paper, glass bottles and plastic bottles) from the Site. Materials recovered will be sold for recycling.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	-
S8.5	To avoid any odour and litter impact, accurate number of portable toilets will be provided for workers on-site.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	The burning of refuse on construction sites is prohibited by law.	All area/ During construction	Contractor(s)		✓		Implemented	Air Pollution Control Ordinance (Cap 311)
S8.7	To facilitate monitoring and control over the contractors' performance on waste management, a waste inspection and audit	All facilities/ During construction	ET/ IEC		✓		Implemented	-

**Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	programme will be implemented throughout the construction phase.							

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
Ecology								
S9.7	For slope mitigation works within the Clear Water Bay Country Park, to avoid tree felling and damages to trees, the exact locations of the flexible barrier foundation plates, soil nails and rock dowels can be adjusted during detailed design, and a setback distance from existing trees is recommended to be maintained as far as practical. A detailed specification describing the exact locations of the flexible barrier foundation plates, soil nails and rock dowels will be prepared to illustrate how the setback distance from existing trees would be implemented for tree avoidance.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		Implemented	-
S9.7	Pruning of tree canopies along the alignment of the flexible barriers shall be limited to a minimum.	Slope mitigation works area/ During construction	Contractor(s)		✓		Implemented	
S9.7	The alignment of flexible barriers shall be optimized to preserve all species of conservation interest and minimize the impact to the existing vegetation as far as practicable. All individuals of <i>Marsdenia lachnostoma</i> within the slope mitigation areas shall be retained <i>in-situ</i> , by positioning the alignment of flexible barrier at a minimum 1.5m in a radius away from these individuals.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		N/A	-
S9.7 and 9.10	At the detailed design stage prior to the commencement of the slope mitigation works, a vegetation survey shall be carried out at the slope mitigation areas within the Clear Water Bay Country Park to assess the condition and identify the location of each individual of <i>Marsdenia lachnostoma</i> and other flora species of conservation interest that may be directly affected by the construction works.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		N/A	-
S9.7	Temporary fencing will be installed to fence off	Slope mitigation works	Contractor(s)		✓		N/A	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	the concerned species either in groups of individually within the works area and in the close proximity to prevent from being damaged and disturbed during construction. A sign identifying the site shall be attached to the fence and flagging tape shall be attached to the individuals to visualize their locations.	area/ During construction						
S9.7 and S9.10	A specification for fencing and demarcating individuals of <i>Marsdenia lachnostoma</i> (or other flora species of conservation interest, if found) adjacent to the proposed alignment of the flexible barriers will be prepared to protect the species.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Induction training shall also be provided to all site personnel in order to brief them on this flora of conservation interest including the locations and their importance.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-
S9.7	The resident site supervisory staff will closely monitor the conditions of concerned individuals during construction of flexible barriers in the close proximity.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Erect fences along the boundary of the works area before the commencement of works to prevent vehicle movements and encroachment of personnel onto adjacent areas.	All area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	Regularly check the work site boundaries to ensure that they are not breached and that damage does not occur to surrounding areas.	All area/ During construction	Contractor(s)/ Environmental Team (ET)		✓		Implemented	-
S9.7	Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the surrounding habitats through proper management of waste disposal.	All area/ During construction	Contractor(s)		✓		Implemented	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S9.7	Reinstate temporarily affected areas, particularly the habitats of plantation and shrubland-grassland immediately after completion of construction works, through on-site tree/shrub planting. The tree/shrub species will be chosen with reference to those in the surrounding area.	All area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Affected habitats within the Clear Water Bay Country Bay shall be reinstated by hydro-seeding and planting of climbers and native shrub seedlings where practical upon completion of the slope mitigation works.	All area/ During construction	Contractor(s)		✓		N/A	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
Landscape & Visual								
S11.10 & 11.11	The construction area and area allowed for temporary structures, such as the contractor's office, will be minimized to a practical minimum. (MM1)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	At the detailed design stage, the design team will seek to minimize the landscape footprint of the Project and above ground facilities, while satisfying all other requirements. (MM2)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	Design principles will be adopted to take into account the surrounding area, particularly Clear Water Bay Country Park behind and the nearby waterfront, with due consideration given to: - green roofs where practical (ie without equipment on the roof); - roadside planting; - aesthetic treatment of all structures; - vertical greening; screen planting along application site; and - landscape enhancement with amenity planting where practical including planting along the edge (site boundary) fence with native shrubs where feasible, - to reduce their visual impact and blend them into the surrounding landscape. (MM3)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	All trees within the Project Site or the potential slope mitigation works area will be carefully protected during construction according to DEVB TCW No. 10/2013 – Tree Preservation (MM4)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	ETWB TCW No. 3/2006 - Tree Preservation.
S11.10 & 11.11	No tree within the Country Park will be felled. Trees within the Site unavoidably affected by the works will be transplanted where necessary and practical. For trees that need to be felled, compensatory planting will be provided to the satisfaction of relevant Government	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	DEVB TC(W) No. 10/2013

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	departments. A compensatory tree planting proposal including locations of tree compensation will be submitted to seek relevant government department's approval, in accordance with DEVB TC(W) No. 10/2013. (MM5)							
S11.10 & 11.11	Any slope mitigation works necessary to address natural terrain hazards, will be minimized to minimize any potential environmental impact to the Country Park e.g. soil nailing and rock stabilization will aim to avoid existing trees e.g. should any restoration of vegetation be necessary, the best planting matrix with native species will be established, with the aim of resembling the existing vegetation. (MM6)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	N/A	
S11.10 & 11.11	Dredging works for the installation of intake structures and outfall diffusers should be minimized to avoid or reduce any potential environmental impacts to as low as reasonably practicable (ALARP). The intake and outfall structures (e.g. intake openings and diffuser heads) will be prefabricated and transferred to site for installation. (MM7)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	N/A	
S11.10 & 11.11	All night-time lighting will be reduced to a practical minimum both in terms of number of level and will be hooded and directional. (MM8)units and lux level and will be hooded and directional. (MM8)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
Landfill Gas Hazard								
S12.7	During all works, safety procedures should be implemented to minimise the risks of fires and explosions, asphyxiation of workers and toxicity effects resulting from contact with contaminated soil and groundwater.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	During trenching and excavation as well as creation of confined spaces at near to or below ground level, precautions should be clearly laid down and rigidly Gas detection equipment and appropriate breathing apparatus should be available and used when entering confined spaces or trenches deeper than 1 metre.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	The Contractor should make the workers are aware of potential hazards of working in confined spaces (any chamber, manhole or culvert which is large enough to permit access to personnel). Such work in confined spaces is controlled by the Factories and Industrial Undertakings (Confined Spaces) Regulations of the Factories and Industrial Undertakings Ordinance. Following the Safety Guide to Working in Confined Spaces ensures compliance with the above regulations.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Safety officers, specifically trained with regard to landfill gas and leachate related hazards and the appropriate actions to take in adverse circumstances, should be present on the site throughout the works, in particular, when works are undertaken below grade.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	All personnel who work on site and all visitors to the site should be made aware of the possibility of ignition of gas in the vicinity of the works, the possible presence of contaminated water and the need to avoid physical contact with it.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S12.7	Monitoring for landfill gas should be undertaken in all excavations, manholes, chambers (particularly during pipe jacking) and any confined spaces through the use of an intrinsically safe portable instrument, appropriately calibrated and capable of measuring the concentrations of methane, carbon dioxide and oxygen.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Monitoring frequency and areas to be monitored should be specified prior to commencement of groundwork, either by the Safety Officer, or by an appropriately qualified person. All measurements should be recorded and documented.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Proceed drilling with adequate care and precautions against the potential hazards which may be encountered.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Prior to the commencement of the site works, the drilling contractor should devise a 'method-of-working' statement covering all normal and emergency procedures (including but not limited to number of operatives, experience and special skills of operatives, normal method of operations, emergency procedures, supervisors responsibilities, storage and use of safety equipment, safety procedures and signs, barriers and guarding). The site supervisor and all operatives must be familiar with this statement.	All area/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Where below ground service entries are necessary to the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II), the entry point should be sealed to prevent gas entry. In addition, any below grade cable trenches entering the Incoming Switchgear Room and 132 kV Substation can become the	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	pathway for landfill gas and hence gridded metal covers should be used.							
S12.7	It is recommended regular landfill gas monitoring should be carried out at the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II). The monitoring frequency will be monthly for the first year of operation. If the monitoring results show no sign of landfill gas migration, reduce the monitoring frequency to once every six months.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	
S12.7	The manholes and utility pits within the Project Site and along the fresh water mains. Each manhole/ utility pit should be monitored with two measurements (at mid depth and base). Each measurement should be monitored for a minimum of 10 minutes. A steady reading and peak reading should be recorded at each manhole/ utility pit and for each measurement. The need for venting the manhole/ utility pit and further monitoring will be reviewed after the initial monitoring.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	All construction, operation and maintenance personnel working on-site as well as visitors should be made aware of the hazards of landfill gas and its possible presence on-site. This should be achieved through a combination of posting warning signs in prominent places and also by access to detailed information on landfill gas hazards and the designs and procedural means by which these hazards are being minimized on-site.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	

Note: D – Design stage C – Construction O – Operation

Appendix D

Impact Monitoring Schedule of the Reporting Month

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Nov-20						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
1	2	3	4	5	6 Impact Monitoring	7
8	9	10	11	12 Impact Monitoring	13	14
15	16	17	18 Impact Monitoring	19	20	21
22	23	24	25	26	27 Impact Monitoring	28
29	30					

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Appendix E

Noise Monitoring Equipment Calibration Certificate

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



綜合試驗有限公司
SOILS & MATERIALS ENGINEERING CO., LTD.
 香港新界葵涌永基路22-24號椰林閣集團大廈全幢
 The Whole Block of YLK Group Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong.
 Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com



CERTIFICATE OF CALIBRATION

Certificate No.: 20CA0803 01 Page: 1 of 2

Item tested

Description: Acoustical Calibrator (Class 1)
 Manufacturer: Pulsar Instruments Ltd.
 Type/Model No.: 105
 Serial/Equipment No.: 63705
 Adaptors used: -

Item submitted by

Customer: Acuity Sustainability Consulting Limited.
 Address of Customer: -
 Request No.: -
 Date of receipt: 03-Aug-2020

Date of test: 06-Aug-2020

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2341427	11-May-2021	SCL
Preamplifier	B&K 2673	2743150	03-Jun-2021	CEPREI
Measuring amplifier	B&K 2610	2346941	03-Jun-2021	CEPREI
Signal generator	DS 360	33873	19-May-2021	CEPREI
Digital multi-meter	34401A	US36087050	19-May-2021	CEPREI
Audio analyzer	8903B	GB41300350	18-May-2021	CEPREI
Universal counter	53132A	MY40003662	18-May-2021	CEPREI

Ambient conditions

Temperature: 22 ± 1 °C
 Relative humidity: 55 ± 10 %
 Air pressure: 1005 ± 5 hPa



Test specifications

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.

Approved Signatory:  Date: 07-Aug-2020 Company Chop: 

Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



Certificate of Calibration

for

Description: Sound Level Meter
Manufacturer: NTi Audio
Type No.: XL2 (Serial No.: A2A-13548-E0)
Microphone: ACO 7052 (Serial No.:73780)
Preamplifier: NTi Audio MA220 (Serial No.:5235)

Submitted by:

Customer: Acuity Sustainability Consulting Limited
Address: Unit 1908, iPlace, Nos. 301-305 Castle Peak Road,
Kwai Chung, New Territories

Upon receipt for calibration, the instrument was found to be:

- Within
 Outside

the allowable tolerance.

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 6 January 2020

Date of calibration: 10 January 2020

Calibrated by: 
Calibration Technician

Certified by: 
Tang Cheuk Hang
Quality Manager

Date of issue: 10 January 2020

Certificate No.: APJ19-143-CC001



Page 1 of 4



1. Calibration Precaution:

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

2. Calibration Conditions:

Air Temperature: 23.0 °C
 Air Pressure: 1006 hPa
 Relative Humidity: 71.0 %

3. Calibration Equipment:

	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV180064	HOKLAS

4. Calibration Results

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	1000	94.0	+0.4


Linearity

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	1000	94.0	Ref
				104		104.0	±0.3
				114		114.0	±0.3

Time Weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	1000	94.0	Ref
			Slow			94.0	±0.3

Certificate No.: APJ19-143-CC001



Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong
 Tel: (852) 2668 3423 Fax: (852) 2668 6946
 Homepage: <http://www.aa-lab.com> E-mail: inquirv@aa-lab.com



Frequency Response

Linear Response

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dB	SPL	Fast	94	31.5	94.0	±2.0
					63	94.1	±1.5
					125	94.1	±1.5
					250	94.0	±1.4
					500	94.0	±1.4
					1000	94.0	Ref
					2000	93.8	±1.6
					4000	93.4	±1.6
				8000	92.4	+2.1; -3.1	

A-weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	31.5	54.8	-39.4±2.0
					63	67.9	-26.2±1.5
					125	78.0	-16.1±1.5
					250	85.4	-8.6±1.4
					500	90.8	-3.2±1.4
					1000	94.0	Ref
					2000	95.0	+1.2±1.6
					4000	94.4	+1.0±1.6
				8000	91.3	-1.1±2.1; -3.1	

C-weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBC	SPL	Fast	94	31.5	91.0	-3.0±2.0
					63	93.3	-0.8±1.5
					125	93.9	-0.2±1.5
					250	94.1	-0.0±1.4
					500	94.1	-0.0±1.4
					1000	94.0	Ref
					2000	93.6	-0.2±1.6
					4000	92.6	-0.8±1.6
				8000	89.4	-3.0±2.1; -3.1	

Certificate No.: APJ19-143-CC001



Page 3 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong
 Tel: (852) 2668 3423 Fax: (852) 2668 6946
 Homepage: <http://www.aa-lab.com> E-mail: inquirv@aa-lab.com



5. Calibration Results Applied

The results apply to the particular unit-under-test only. All calibration points are within manufacture's specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.10
	63 Hz	± 0.05
	125 Hz	± 0.10
	250 Hz	± 0.10
	500 Hz	± 0.10
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	± 0.05
	8000 Hz	± 0.10
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

Note:

The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)*L shall not be liable for any loss or damage resulting from the use of the equipment.



Certificate No.: APJ19-143-CC001

Page 4 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong
 Tel: (852) 2668 3423 Fax: (852) 2668 6946
 Homepage: <http://www.aa-lab.com> E-mail: inquirv@aa-lab.com

Appendix F

Event/Action Plan for Noise Exceedance

Event and Action Plan for Construction Noise Monitoring

Event	Action			
	ET	IEC	ER	Contractor
Action Level	<ol style="list-style-type: none"> 1. Carry out investigation to identify the source and cause of the complaint/ exceedance(s) 2. Notify IEC, ER, and Contractor and report the results of investigation to the Contractor, ER and the IEC 3. Discuss with the Contractor and IEC for remedial measures required 4. If the complaint is related to the Project, conduct additional monitoring for checking mitigation effectiveness and report the findings and results to the IEC, ER and the Contractor 	<ol style="list-style-type: none"> 1. Review the analyzed results submitted by the ET 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly 3. Supervise the implementation of remedial measures 	<ol style="list-style-type: none"> 1. Confirm receipt of Notification of Exceedance in writing 2. Require Contractor to propose remedial measures for the analysed noise problem 3. Ensure remedial measures are properly implemented 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals, if required, to the IEC and ER 2. Implement noise mitigation proposals.

Appendix G

Noise Monitoring Data

Date	Time	Weather	Leq-5min, dB(A)						Leq-30min, dB(A)	Leq30 (min) L ₁₀ dB(A)	Leq30 (min) L ₉₀ dB(A)	Limit Level, dB(A)
			Reading (1)	Reading (2)	Reading (3)	Reading (4)	Reading (5)	Reading (6)				
06/11/2020	11:20 - 11:50	Sunny	59.2	60.8	61.5	61.1	59.6	59.9	60.4	62.3	58.4	70.0
12/11/2020	10:38 - 11:08	Sunny	61.1	60.2	60.8	61.6	61.3	61.4	61.1	62.8	57.5	70.0
18/11/2020	10:35 - 11:05	Sunny	58.4	60.5	60.9	59.4	59.7	61.9	60.3	62.1	57.1	70.0
27/11/2020	15:10 - 15:40	Sunny	59.7	60.4	60.5	58.8	59.4	60.9	60.0	62.5	55.8	70.0

No examination was scheduled in the reporting month. Hence the noise limit level will be 70.0 dB(A) Academic School Calendar can be found in Appendix O.



6/11/2020



12/11/2020



18/11/2020



27/11/2020

Appendix H

Waste Flow Table

Monthly Summary Waste Flow Table

Name of Department: WSD Contract No. / Works Order No.: 13/WSD/16

Monthly Summary Waste Flow Table for November 2020

Month	Actual Quantities of <u>Inert</u> Construction Waste Generated Monthly					
	Total Quantity Generated (see Note 4)	Hard Rock and Large Broken Concrete (see Note 3)	Reused in the Contract	Reused in other Projects	Disposed of as Public Fill	Imported Fill (see Note 1)
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)
2018	1.157	0.063	0.000	0.000	1.157	0.518
2019	5.178	0.043	2.211	0.000	2.520	3.200
Jan 2020	0.153	0.003	0.000	0.000	0.153	0.077
Feb 2020	0.186	0.010	0.000	0.000	0.186	0.170
Mar 2020	0.282	0.005	0.000	0.000	0.282	0.201
Apr 2020	0.497	0.016	0.000	0.000	0.497	0.069
May 2020	1.294	0.306	0.291	0.000	1.003	0.030
Sub-total	2.412	0.340	0.291	0.000	2.121	0.547
Jun 2020	0.948	0.076	0.000	0.000	0.948	0.200
Jul-2020	1.514	0.021	0.000	0.000	1.514	0.075
Aug-2020	1.272	0.071	0.000	0.000	1.272	0.111
Sep-2020	1.423	0.148	--	--	1.423	0.026
Oct-2020	1.470	0.120	--	--	1.470	0.025
Nov-2020	2.180	0.340	--	--	2.176	0.152
Total for 2020	11.219	1.116	0.291	0.000	10.924	1.136

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Month	Actual Quantities of <u>Non-inert</u> Construction Waste Generated Monthly				
	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. General Refuse disposed at Landfill
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
2018	0.000	0.417	0.000	0.000	0.139
2019	0.000	0.062	0.000	0.000	0.102
Jan 2020	0.000	0.055	0.000	0.000	0.002
Feb 2020	0.000	0.050	0.000	0.000	0.001
Mar 2020	0.000	0.052	0.000	0.000	0.001
April 2020	0.000	0.043	0.000	0.000	0.002
May 2020	0.000	0.058	0.000	0.000	0.020
Sub-total	0.000	0.258	0.000	0.000	0.026
Jun-2020	0.000	0.057	0.000	0.000	0.003
Jul-2020	0.000	0.050	0.000	0.000	0.001
Aug-2020	0.000	0.048	0.000	0.000	0.000
Sep-2020	0.000	0.045	0.000	0.000	0.003
Oct-2020	0.000	0.040	0.000	0.000	0.002
Nov-2020	0.000	0.056	0.000	0.000	0.003
Total for 2020	0.000	0.554	0.000	0.000	0.038

Notes:

1. The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
2. Plastic refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
3. Broken concrete for recycling into aggregate.

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



4. “Total Quantity Generated” only refers to the actual quantities of inert C&D materials generated monthly excluding those that will be recycled (Hard Rock and Large Broken Concrete, Reused in the Contract, Reused in other Projects). Imported fill will not be included in “Total Quantity Generated” as those C&D materials are not generated from this project.
5. C&D materials in tonnes are converted to meter cube (m³) on a scale of 0.5.
6. Source and types of Imported Fill in the reporting month
 - i. K. Wah Quarry Company Limited: (Soil) 113.275m³ (226.55 tonnes/9 cars)
 - ii. K. Wah Quarry Company Limited: (Sub-base Materials) 38.89m³ (77.78 tonnes/3 cars)
7. The amount of Hard Rock and Large Broken Concrete are disposed to public fill, the breakdown of C&D materials disposed to public fill is shown as below:

Type of C&D Materials	Description of C&D Materials	C&D Waste Disposed (Volume) (m ³)
Inert	Bentonite	4.60
	Broken Concrete	224.55
	Broken Rock	127.85
	Mixed Construction Waste (>50% inert)	--
	Building Debris	16.50
	Mixed Rock and Soil	1312.15
	Reclaimed Asphalt Pavement	417.90
	Slurry	20.70
	Soil	52.40
	TOTAL =	2176.65
Non-inert	TOTAL =	3.40

Appendix I

**Landfill
Equipment
Certificate**

Gas

**Monitoring
Calibration**



香港新界葵涌葵昌路58-70號永祥工業大廈10樓B室
 Unit B, 10/F., Wing Cheung Industrial Building, 58-70 Kwai Cheong Road, Kwai Chung, New Territories, HK
 Tel: (852) 2751 7770 Fax: (852) 2756 2051 E-mail: rotter@rotter.com.hk

Calibration Report - Gas Detector

PGM-2500 (QRAE III) --- LEL/O2/CO/H2S

UNIT INFORMATION :

Customer:	Penta Ocean Construction Co Ltd	Serial # :	M02A016735	Model :	QRAE III
		Firmware :	V2.14	Sensor :	LEL/O2/CO/H2S
		Cal date :	28-Jul-2020	Inspected:	Teddy

SENSOR DATA :

	LEL sensor (ME)	O2 sensor	CO sensor (Tox1)	H2S sensor (Tox2)
Calibration dates:	28-Jul-2020	28-Jul-2020	28-Jul-2020	28-Jul-2020
After Calibration levels	50%	18.00%	50 ppm	10.1 ppm
Alarm levels (Low):	10.00%	19.50%	35 ppm	10 ppm
Alarm levels (High):	20.00%	23.50%	200 ppm	20 ppm
TWA Level :	--	--	35 ppm	10 ppm
STEL Level :	--	--	100 ppm	15 ppm

Status:

Pump Speed	Low	Back Light	Manual
Clock	Yes	Measure	Average

LEL Gas Selection

LEL Calibration Gas	Methane	LEL measurement Gas	Methane
LEL Custom Gas	LEL_custom_gas	LEL Custom Factor	1.0


Gas types used : 4-Gas Mix: (18% O2, 50ppm CO, 10ppm H2S, 50% LEL CH4, BAL N2) Gas lot #13333090 Cyl# 18
 *** Fresh Air Calibration is highly recommended to proceed prior for measurement each time.

Replaced Parts:

Notes:

The unit was calibrated and checked under good working condition

**Next calibration date on or before 27 July 2021

Serviced by  Teddy Wong
 Rotter International Ltd

Appendix J

Landfill Gas Monitoring Data

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2600 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	2-11-2020	0830	Fine	0	0	0	20.9	24 / 1016	2.5
	2-11-2020	1330	Fine	0	0	0	20.9	28 / 1013	2.5
	2-11-2020	1700	Fine	0	0	0	20.9	27 / 1013	2.5
Area B	2-11-2020	0845	Fine	0	0	0	20.9	24 / 1016	2.5
	2-11-2020	1345	Fine	0	0	0	20.9	28 / 1013	2.5
	2-11-2020	1645	Fine	0	0	0	20.9	27 / 1013	2.5

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		2-11-2020
Laboratory Staff:			
Checked by:	Chun-yen Au (Senior Foreman)		2-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-25C0 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.FC 4950	2/11/2020	0855	Fine	0	0	0	20.9	24/1016	2.2
	2/11/2020	1355	Fine	0	0	0	20.9	28/1017	2.5
CH.FC 0490	2/11/2020	0920	Fine	0	0	0	20.9	24/1016	2.5
	2/11/2020	1400	Fine	0	0	0	20.9	28/1017	2.5
Pit C	2/11/2020	0915	Fine	0	0	0	20.9	24/1016	8
	2/11/2020	1415	Fine	0	0	0	20.9	28/1017	8
157CHCT 2+66	2/11/2020	0930	Fine	0	0	0	20.9	24/1016	3.1
	2/11/2020	1435	Fine	0	0	0	20.9	28/1017	3.1
157 Pit C	2/11/2020	0945	Fine	0	0	0	20.9	25/1016	1.4
	2/11/2020	1445	Fine	0	0	0	20.9	28/1017	1.4
157 Pit B	2/11/2020	0955	Fine	0	0	0	20.9	25/1016	1
	2/11/2020	1455	Fine	0	0	0	20.9	28/1017	1
WPK 1	2/11/2020	1015	Fine	0	0	0	20.9	25/1016	2.2
	2/11/2020	1515	Fine	0	0	0	20.9	28/1017	2.2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		2/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mba)	Remark Depth (m)
CHA 670	2/11/2020	1025	Fine	0	0	0	20.9	25/1016	2.5
	2/11/2020	1525	Fine	0	0	0	20.9	28/1012	3.5
WPR-3	2/11/2020	1035	Fine	0	0	0	20.9	25/1016	4.2
	2/11/2020	1535	Fine	0	0	0	20.9	28/1012	4.2
Pit B	2/11/2020	1055	Fine	0	0	0	20.9	25/1016	2
	2/11/2020	1555	Fine	0	0	0	20.9	28/1012	2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		2/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	3-11-2020	0830	Fine	0	0	0	20.9	22/1018	2.5
	3-11-2020	1330	Fine	0	0	0	20.9	25/1015	2.5
	3-11-2020	1700	Fine	0	0	0	20.9	24/1015	2.5
Area B	3-11-2020	0845	Fine	0	0	0	20.9	22/1018	2.5
	3-11-2020	1345	Fine	0	0	0	20.9	25/1015	2.5
	3-11-2020	1645	Fine	0	0	0	20.9	24/1015	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		3-11-2020
Laboratory Staff:			
Checked by:	Sheng-fen (Senior Foreman) Lau		3-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	26 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.FC 45c	3/11/2020	0835	Fine	0	0	0	20.9	22/1028	2.5
	3/11/2020	1355	Fine	0	0	0	20.9	25/1015	2.5
CH.FC 049c	3/11/2020	0900	Fine	0	0	0	20.9	22/1015	2.5
	3/11/2020	1455	Fine	0	0	0	20.9	25/1015	2.5
Pit C	3/11/2020	0915	Fine	0	0	0	20.9	22/1028	1
	3/11/2020	1415	Fine	0	0	0	20.9	25/1025	1
137CHC1 2466	3/11/2020	0935	Fine	0	0	0	20.9	22/1018	2.1
	3/11/2020	1435	Fine	0	0	0	20.9	25/1015	2.1
137 Pit C	3/11/2020	0945	Fine	0	0	0	20.9	22/1028	1.4
	3/11/2020	1445	Fine	0	0	0	20.9	25/1015	1.4
137 Pit B	3/11/2020	0955	Fine	0	0	0	20.9	22/1018	1
	3/11/2020	1455	Fine	0	0	0	20.9	25/1015	1
WPR 1	3/11/2020	1015	Fine	0	0	0	20.9	23/1028	2.2
	3/11/2020	1315	Fine	0	0	0	20.9	24/1025	2.2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		3/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PCM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHA 6470	3/11/2020	1025	Fine	0	0	0	20.9	23 / 1017	3.5
	3/11/2020	1525	Fine	0	0	0	20.8	24 / 1015	3.5
WPR 3	3/11/2020	1045	Fine	0	0	0	20.9	24 / 1017	4.2
	3/11/2020	1335	Fine	0	0	0	20.9	24 / 1015	4.2
Pit B	3/11/2020	1055	Fine	0	0	0	20.9	23 / 1017	8
	3/11/2020	1555	Fine	0	0	0	20.9	24 / 1015	8

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		3/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	26 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	4-11-2020	0830	Fine	0	0	0	20.9	22 / 1018	2.5
	4-11-2020	1330	Fine	0	0	0	20.9	24 / 1016	2.5
	4-11-2020	1700	Fine	0	0	0	20.9	23 / 1016	2.5
Area B	4-11-2020	0845	Fine	0	0	0	20.9	22 / 1018	2.5
	4-11-2020	1345	Fine	0	0	0	20.9	24 / 1016	2.5
	4-11-2020	1645	Fine	0	0	0	20.9	23 / 1016	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		4-11-2020
Laboratory Staff:			
Checked by:	(Senior Foreman) Eric		4-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PCM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4+50	4/11/2020	0855	Fine	0	0	0	20.9	23/1018	2.5
CHFC 0+40	4/11/2020	1255	Fine	0	0	0	20.9	24/1016	2.5
	4/11/2020	0935	Fine	0	0	0	20.9	23/1018	2.5
P+C	4/11/2020	1400	Fine	0	0	0	20.9	24/1016	2.5
	4/11/2020	0915	Fine	0	0	0	20.9	23/1018	8
MCHC 2+66	4/11/2020	1455	Fine	0	0	0	20.9	24/1016	8
	4/11/2020	0935	Fine	0	0	0	20.9	24/1018	3.1
137 P+C	4/11/2020	1435	Fine	0	0	0	20.9	24/1016	3.1
	4/11/2020	0945	Fine	0	0	0	20.9	24/1018	1.4
137 P+B	4/11/2020	1445	Fine	0	0	0	20.9	24/1016	1.4
	4/11/2020	0935	Fine	0	0	0	20.9	24/1018	1
WPC 1	4/11/2020	1455	Fine	0	0	0	20.9	24/1016	1
	4/11/2020	1015	Fine	0	0	0	20.9	24/1018	2.2
	4/11/2020	1115	Fine	0	0	0	20.9	23/1016	2.2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		4/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHA 670	4/11/2020	1225	Fine	0	0	0	20.9	24/1018	3.5
	4/11/2020	1825	Fine	0	0	0	20.9	23/1016	3.8
WRB 3	4/11/2020	1225	Fine	0	0	0	20.9	24/1018	4.2
	4/11/2020	1555	Fine	0	0	0	20.9	23/1016	4.2
Pit B	4/11/2020	1225	Fine	0	0	0	20.9	24/1018	8
	4/11/2020	1555	Fine	0	0	0	20.9	23/1016	8
								/	
								/	
								/	
								/	
								/	
								/	
								/	

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		4/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PCM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	5-11-2020	0830	Fine	0	0	0	20.9	22 / 1014	2.5
	5-11-2020	1330	Fine	0	0	0	20.9	24 / 1016	2.5
	5-11-2020	1720	Fine	0	0	0	20.9	24 / 1016	2.5
Area B	5-11-2020	0845	Fine	0	0	0	20.9	22 / 1014	2.5
	5-11-2020	1345	Fine	0	0	0	20.9	24 / 1016	2.5
	5-11-2020	1645	Fine	0	0	0	20.9	24 / 1016	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		5-11-2020
Laboratory Staff:			
Checked by:	Chen Yuen Lau (Senior Foreman) Lau		5-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
FGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4130	5/11/2020	0835	Fine	0	0	0	20.9	22/1018	2.5
	5/11/2020	1335	Fine	0	0	0	20.9	24/1016	2.5
CHFC 4140	5/11/2020	0900	Fine	0	0	0	20.9	22/1018	2.5
	5/11/2020	1400	Fine	0	0	0	20.9	24/1016	2.5
P1C	5/11/2020	0915	Fine	0	0	0	20.9	22/1018	8
	5/11/2020	1415	Fine	0	0	0	20.9	24/1018	8
137CHC 2166	5/11/2020	0935	Fine	0	0	0	20.9	22/1018	7.1
	5/11/2020	1435	Fine	0	0	0	20.9	24/1018	7.1
137 P1C	5/11/2020	0945	Fine	0	0	0	20.9	22/1018	1.6
	5/11/2020	1445	Fine	0	0	0	20.9	24/1018	1.6
137 P1B	5/11/2020	0955	Fine	0	0	0	20.9	23/1018	1
	5/11/2020	1455	Fine	0	0	0	20.9	24/1018	1
WPR 1	5/11/2020	1015	Fine	0	0	0	20.9	23/1018	2.2
	5/11/2020	1515	Fine	0	0	0	20.9	24/1018	2.2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		5/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE II)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHA 6#10	5/11/2020	1025	Fine	0	0	0	20.9	23/1017	3.5
	5/11/2020	1525	Fine	0	0	0	20.9	24/1015	3.5
WPR 3	5/11/2020	1035	Fine	0	0	0	20.9	23/1017	4.2
	5/11/2020	1335	Fine	0	0	0	20.9	24/1015	4.2
Pit B	5/11/2020	1045	Fine	0	0	0	20.9	23/1017	8
	5/11/2020	1535	Fine	0	0	0	20.9	24/1015	8
								/	
								/	
								/	
								/	
								/	
								/	
								/	

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		5/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	6-11-2020	0830	Fine	0	0	0	20.9	22/1018	2.5
	6-11-2020	1330	Fine	0	0	0	20.9	27/1014	2.5
	6-11-2020	1730	Fine	0	0	0	20.9	26/1013	2.5
Area B	6-11-2020	0845	Fine	0	0	0	20.9	22/1018	2.5
	6-11-2020	1345	Fine	0	0	0	20.9	27/1014	2.5
	6-11-2020	1645	Fine	0	0	0	20.9	26/1013	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		6-11-2020
Laboratory Staff:			
Checked by:	Chun yan Lau (Senior Foreman) Lau		6-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
FGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4SD	6/11/2020	0835	Fine	0	0	0	20.9	23 / 1018	2.3
	6/11/2020	1335	Fine	0	0	0	20.9	23 / 1018	2.3
CHFC 27A0	6/11/2020	0900	Fine	0	0	0	20.9	23 / 1018	2.3
	6/11/2020	1400	Fine	0	0	0	20.9	23 / 1018	2.3
P1C	6/11/2020	0915	Fine	0	0	0	20.9	23 / 1018	1
	6/11/2020	1415	Fine	0	0	0	20.9	26 / 1018	1
137CHC1466	6/11/2020	0935	Fine	0	0	0	20.9	23 / 1018	3.1
	6/11/2020	1435	Fine	0	0	0	20.9	26 / 1018	3.1
137 P1C	6/11/2020	0945	Fine	0	0	0	20.9	23 / 1018	1.4
	6/11/2020	1445	Fine	0	0	0	20.9	26 / 1018	1.4
137 P1B	6/11/2020	0955	Fine	0	0	0	20.9	24 / 1018	1
	6/11/2020	1455	Fine	0	0	0	20.9	26 / 1018	1
WPR1	6/11/2020	1015	Fine	0	0	0	20.9	23 / 1018	2.2
	6/11/2020	1515	Fine	0	0	0	20.9	26 / 1018	2.2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		6/11/2020
Laboratory Staff:			
Checked by:			

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CWA 6+70	6/11/2020	1025	Fine	0	0	0	20.9	25/1017	3.5
	6/11/2020	1325	Fine	0	0	0	20.9	26/1019	3.5
W&R 3	6/11/2020	1055	Fine	0	0	0	20.9	25/1017	4.2
	6/11/2020	1355	Fine	0	0	0	20.9	26/1017	4.2
Pit B	6/11/2020	1055	Fine	0	0	0	20.9	25/1017	8
	6/11/2020	1555	Fine	0	0	0	20.9	26/1019	8

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		6/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	26 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	7-11-2020	0830	Fine	0	0	0	20.9	25 / 1016	2.5
	7-11-2020	1330	Fine	0	0	0	20.9	29 / 1013	2.5
	7-11-2020	1700	Fine	0	0	0	20.9	29 / 1013	2.5
Area B	7-11-2020	0845	Fine	0	0	0	20.9	25 / 1016	2.5
	7-11-2020	1345	Fine	0	0	0	20.9	29 / 1013	2.5
	7-11-2020	1645	Fine	0	0	0	20.9	29 / 1013	2.5

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent (RenoPipe))		7-11-2020
Laboratory Staff:			
Checked by:	Chan yan kwai (Senior Foreman)		7-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
 Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE II)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4+50	7/11/2020	0833	Fine	0	0	0	20.9	28 / 1016	2.5
	7/11/2020	1333	Fine	0	0	0	20.9	30 / 1013	2.5
CHFC 6+60	7/11/2020	0900	Fine	0	0	0	20.9	28 / 1016	2.5
	7/11/2020	1400	Fine	0	0	0	20.9	30 / 1013	2.5
Pit C	7/11/2020	0915	Fine	0	0	0	20.9	28 / 1016	0
	7/11/2020	1415	Fine	0	0	0	20.9	30 / 1013	0
137CHC1266	7/11/2020	0930	Fine	0	0	0	20.9	26 / 1016	2.1
	7/11/2020	1430	Fine	0	0	0	20.9	30 / 1013	2.1
137 P1C	7/11/2020	0945	Fine	0	0	0	20.9	26 / 1016	1.4
	7/11/2020	1445	Fine	0	0	0	20.9	30 / 1013	1.4
137 P1B	7/11/2020	0955	Fine	0	0	0	20.9	26 / 1016	1
	7/11/2020	1455	Fine	0	0	0	20.9	30 / 1013	1
WPK 1	7/11/2020	1015	Fine	0	0	0	20.9	27 / 1016	2.2
	7/11/2020	1515	Fine	0	0	0	20.9	30 / 1013	2.2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		7/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Datcs calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHA 670	7/11/2020	1025	Fine	0	0	0	20.9	27 / 1016	3.5
	7/11/2020	1520	Fine	0	0	0	20.9	30 / 1015	3.5
WPP 3	7/11/2020	1030	Fine	0	0	0	20.9	27 / 1016	4.2
	7/11/2020	1535	Fine	0	0	0	20.9	30 / 1014	4.2
P+B	7/11/2020	1055	Fine	0	0	0	20.9	27 / 1016	8
	7/11/2020	1555	Fine	0	0	0	20.9	29 / 1014	8
								/	
								/	
								/	
								/	
								/	
								/	
								/	
								/	

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		7/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	9-11-2020	0830	Fine	0	0	0	20.9	22 / 1019	2.5
	9-11-2020	1350	Fine	0	0	0	20.9	25 / 1016	2.5
	9-11-2020	1700	Fine	0	0	0	20.9	23 / 1016	2.5
Area B	9-11-2020	0845	Fine	0	0	0	20.9	22 / 1019	2.5
	9-11-2020	1345	Fine	0	0	0	20.9	25 / 1016	2.5
	9-11-2020	1645	Fine	0	0	0	20.9	23 / 1016	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		9-11-2020
Laboratory Staff:			
Checked by:	Chen Yuen Kau (Senior Foreman) Kau		9-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 2450	9/11/2020	0853	Fine	0	0	0	20.9	24/1014	2.5'
	9/11/2020	1355	Fine	0	0	0	20.9	26/1016	2.5'
CHFC 0490	9/11/2020	0800	Fine	0	0	0	20.9	24/1014	2.5'
	9/11/2020	1430	Fine	0	0	0	20.9	26/1016	2.5'
Pit C	9/11/2020	0913	Fine	0	0	0	20.9	24/1014	8
	9/11/2020	1413	Fine	0	0	0	20.9	26/1016	8
137CHC 2460	9/11/2020	0853	Fine	0	0	0	20.9	24/1014	3.1
	9/11/2020	1433	Fine	0	0	0	20.9	26/1016	3.1
137 Pit C	9/11/2020	0944	Fine	0	0	0	20.9	24/1014	1.4
	9/11/2020	1424	Fine	0	0	0	20.9	26/1016	1.4
137 Pit B	9/11/2020	0955	Fine	0	0	0	20.9	24/1014	1
	9/11/2020	1433	Fine	0	0	0	20.9	26/1016	1
WPI-1	9/11/2020	1013	Fine	0	0	0	20.9	24/1014	2.2
	9/11/2020	1513	Fine	0	0	0	20.9	26/1016	2.2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent (RenoPipe))		9/11/2020
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28**



Contract no. 13/WSD/16
Mainlaying in Tseung Kwan O
Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHA 672	9/11/2020	1025	Fine	0	0	0	20.9	24/1016	3.5
	9/11/2020	1025	Fine	0	0	0	20.9	26/1016	3.5
WPE 3	9/11/2020	1035	Fine	0	0	0	20.9	24/1016	4.2
	9/11/2020	1035	Fine	0	0	0	20.9	26/1016	4.2
Pit B	9/11/2020	1045	Fine	0	0	0	20.9	25/1016	8
	9/11/2020	1045	Fine	0	0	0	20.9	26/1016	8
								/	
								/	
								/	
								/	
								/	
								/	

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		9/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE II)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	10-11-2020	0830	Fine	0	0	0	20.9	23 / 1020	2.5
	10-11-2020	1350	Fine	0	0	0	20.9	23 / 1018	2.5
	10-11-2020	1700	Fine	0	0	0	20.9	23 / 1018	2.5
Area B	10-11-2020	0845	Fine	0	0	0	20.9	21 / 1020	2.5
	10-11-2020	1345	Fine	0	0	0	20.9	23 / 1018	2.5
	10-11-2020	1645	Fine	0	0	0	20.9	23 / 1018	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		10-11-2020
Laboratory Staff:			
Checked by:	Chien-jan tau (Senior Foreman)		10-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4450	10/11/2020	0838	Fine	0	0	0	20.9	21 / 1020	2.5
CHFC 2490	10/11/2020	1355	Fine	0	0	0	20.9	23 / 1018	2.5
	10/11/2020	0900	Fine	0	0	0	20.9	21 / 1020	2.5
Pit c	10/11/2020	1405	Fine	0	0	0	20.9	23 / 1018	2.5
	10/11/2020	0915	Fine	0	0	0	20.9	21 / 1020	8
137 CHCT 246	10/11/2020	1415	Fine	0	0	0	20.9	23 / 1018	8
	10/11/2020	0935	Fine	0	0	0	20.9	21 / 1020	7.1
137 Pit c	10/11/2020	1435	Fine	0	0	0	20.9	23 / 1018	3.1
	10/11/2020	0945	Fine	0	0	0	20.9	21 / 1020	1.4
137 Pit B	10/11/2020	1445	Fine	0	0	0	20.9	23 / 1018	1.4
	10/11/2020	0955	Fine	0	0	0	20.9	21 / 1020	1
WPF 1	10/11/2020	1455	Fine	0	0	0	20.9	23 / 1018	1
	10/11/2020	1015	Fine	0	0	0	20.9	22 / 1020	2.2
	10/11/2020	1515	Fine	0	0	0	20.9	23 / 1018	2.2

	Name & Designation	Signature	Date
Field Operator:	Eric Wan (Sub-Agent (RenoPipe))		10/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PCM-2560 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHA 6770	10/11/2020	1025	Fine	0	0	0	20.9	22/1025	3.5
	10/11/2020	1525	Fine	0	0	0	20.9	23/1025	3.5
WPR 5	10/11/2020	1035	Fine	0	0	0	20.9	22/1025	4.2
	10/11/2020	1335	Fine	0	0	0	20.9	23/1025	4.2
Pit B	10/11/2020	1035	Fine	0	0	0	20.9	22/1025	8
	10/11/2020	1335	Fine	0	0	0	20.9	23/1025	8
								/	
								/	
								/	
								/	
								/	
								/	

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		10/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mba)	Remark Depth (m)
Area A	11-11-2020	0830	Fine	0	0	0	20.9	21 / 1021	2.5
	11-11-2020	1350	Fine	0	0	0	20.9	24 / 1019	2.5
	11-11-2020	1700	Fine	0	0	0	20.9	22 / 1019	2.5
Area B	11-11-2020	0845	Fine	0	0	0	20.9	21 / 1021	2.5
	11-11-2020	1345	Fine	0	0	0	20.9	24 / 1019	2.5
	11-11-2020	1645	Fine	0	0	0	20.9	22 / 1019	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent (RenoPipe))		11-11-2020
Laboratory Staff:			
Checked by:	Chan Yan Kiu (Senior Foreman)		11-11-2020

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4+50	11/11/2020	0853	Fine	0	0	0	20.9	21 / 1021	2.5
	11/11/2020	1353	Fine	0	0	0	20.9	23 / 1019	2.5
CHFC 0490	11/11/2020	0900	Fine	0	0	0	20.9	21 / 1021	2.5
	11/11/2020	1400	Fine	0	0	0	20.9	23 / 1019	2.5
PFC	11/11/2020	0915	Fine	0	0	0	20.9	21 / 1021	8
	11/11/2020	1415	Fine	0	0	0	20.9	23 / 1019	8
137CHC1 2+66	11/11/2020	0930	Fine	0	0	0	20.9	21 / 1021	2.1
	11/11/2020	1430	Fine	0	0	0	20.9	23 / 1019	2.1
137 PFC	11/11/2020	0945	Fine	0	0	0	20.9	22 / 1021	1.4
	11/11/2020	1445	Fine	0	0	0	20.9	23 / 1019	1.4
137 PFC B	11/11/2020	0955	Fine	0	0	0	20.9	22 / 1021	1
	11/11/2020	1455	Fine	0	0	0	20.9	23 / 1019	1
WPR	11/11/2020	1015	Fine	0	0	0	20.9	22 / 1021	2.2
	11/11/2020	1515	Fine	0	0	0	20.9	23 / 1019	2.2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		11/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28




Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	26 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
UHA 670	11/11/2020	1025	Fine	0	0	0	20.9	22 / 1024	3.5
WPR 3	11/11/2020	1020	Fine	0	0	0	20.9	27 / 1019	3.5
	11/11/2020	1030	Fine	0	0	0	20.9	22 / 1024	4.2
Pit B	11/11/2020	1335	Fine	0	0	0	20.9	23 / 1019	4.2
	11/11/2020	1055	Fine	0	0	0	20.9	22 / 1024	8
	11/11/2020	1538	Fine	0	0	0	20.9	23 / 1019	8
								/	
								/	
								/	
								/	
								/	
								/	

Name & Designation Signature Date
 Field Operator: Eric Man (Sub-Agent [RenoPipe])  11/11/2020
 Laboratory Staff:
 Checked by:

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	12-11-2020	0830	Fine	0	0	0	20.9	21 / 1020	2.5
	12-11-2020	1530	Fine	0	0	0	20.9	25 / 1017	2.5
	12-11-2020	1700	Fine	0	0	0	20.9	22 / 1017	2.5
Area B	12-11-2020	0845	Fine	0	0	0	20.9	21 / 1020	2.5
	12-11-2020	1345	Fine	0	0	0	20.9	25 / 1017	2.5
	12-11-2020	1645	Fine	0	0	0	20.9	22 / 1017	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		12-11-2020
Laboratory Staff:			
Checked by:	Chan Yan Hau (Senior Foreman) Hau		12-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4450	12/11/2016	0255	Fine	0	0	0	20.9	21/1020	2.5
	12/11/2016	1355	Fine	0	0	0	20.9	24/1017	2.5
CHFC 0490	12/11/2016	0900	Fine	0	0	0	20.9	21/1020	2.5
	12/11/2016	1400	Fine	0	0	0	20.9	24/1017	2.5
Pit C	12/11/2016	0915	Fine	0	0	0	20.9	21/1020	2
	12/11/2016	1415	Fine	0	0	0	20.9	24/1017	2
137CHCT266	12/11/2020	0935	Fine	0	0	0	20.9	22/1020	3.1
	12/11/2020	1435	Fine	0	0	0	20.9	24/1017	3.1
137 Pit C	12/11/2020	0945	Fine	0	0	0	20.9	22/1020	1.4
	12/11/2020	1445	Fine	0	0	0	20.2	24/1017	1.4
137 Pit B	12/11/2020	0955	Fine	0	0	0	20.9	22/1020	1
	12/11/2020	1455	Fine	0	0	0	20.9	24/1017	1
WPR 1	12/11/2020	1015	Fine	0	0	0	20.9	23/1020	2.2
	12/11/2020	1515	Fine	0	0	0	20.9	24/1017	2.2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		12/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring - Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
FGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
HA 6170	12/11/2020	1025	Fine	0	0	0	20.9	23 / 1018	3.5
	12/11/2020	1025	Fine	0	0	0	20.9	24 / 1017	3.5
WR 3	12/11/2020	1055	Fine	0	0	0	20.9	23 / 1018	4.2
	12/11/2020	1055	Fine	0	0	0	20.9	24 / 1017	4.2
P+ B	12/11/2020	055	Fine	0	0	0	20.9	23 / 1018	8
	12/11/2020	1555	Fine	0	0	0	20.9	24 / 1017	8
								/	
								/	
								/	
								/	
								/	
								/	

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		12/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring - Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	13-11-2020	0830	Fine	0	0	0	20.9	22/1018	2.5
	13-11-2020	1530	Fine	0	0	0	20.9	23/1016	2.5
	13-11-2020	1700	Fine	0	0	0	20.9	22/1016	2.5
Area B	13-11-2020	0845	Fine	0	0	0	20.9	22/1018	2.5
	13-11-2020	1345	Fine	0	0	0	20.9	23/1016	2.5
	13-11-2020	1645	Fine	0	0	0	20.9	22/1016	2.5

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		13-11-2020
Laboratory Staff:			
Checked by:	Chen Jianbin (Senior Foreman)		13-11-2020

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring --Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.Fc 4H30	13/11/2020	0825	Fine	0	0	0	20.9	22/1018	2.3
	13/11/2020	135	Fine	0	0	0	20.9	23/1016	2.3
CH.Fc 0H30	13/11/2020	0900	Fine	0	0	0	20.9	22/1018	2.5
	13/11/2020	1400	Fine	0	0	0	20.9	23/1016	2.5
Pit C	13/11/2020	0915	Fine	0	0	0	20.9	22/1018	8
	13/11/2020	1415	Fine	0	0	0	20.9	23/1016	8
137CHCT 2H3	13/11/2020	0830	Fine	0	0	0	20.9	22/1018	7.1
	13/11/2020	1430	Fine	0	0	0	20.9	23/1016	7.1
137 Pit C	13/11/2020	0945	Fine	0	0	0	20.9	23/1018	1.4
	13/11/2020	1445	Fine	0	0	0	20.9	23/1016	1.4
137 Pit B	13/11/2020	0955	Fine	0	0	0	20.9	23/1018	1
	13/11/2020	1455	Fine	0	0	0	20.9	23/1016	1
WR 1	13/11/2020	1015	Fine	0	0	0	20.9	24/1018	2.2
	13/11/2020	1515	Fine	0	0	0	20.9	23/1016	2.2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		13/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-250C (GRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHA 6#10	13/11/2020	1025	Fine	0	0	0	20.9	24/1018	3.5
	13/11/2020	1525	Fine	0	0	0	20.9	23/1016	3.5
WPE 3	13/11/2020	1035	Fine	0	0	0	20.9	24/1018	4.2
	13/11/2020	1535	Fine	0	0	0	20.9	23/1016	4.2
Pit A	13/11/2020	1045	Fine	0	0	0	20.9	24/1018	2
	13/11/2020	1545	Fine	0	0	0	20.9	23/1016	2
Pit B	13/11/2020	1055	Fine	0	0	0	20.9	24/1018	8
	13/11/2020	1555	Fine	0	0	0	20.9	23/1016	8

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		13/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-250C (QRAE II)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	14-11-2020	0830	Fine	0	0	0	20.9	23 / 1018	2.5
	14-11-2020	1330	Fine	0	0	0	20.9	23 / 1017	2.5
Area B	14-11-2020	1700	Fine	0	0	0	20.9	23 / 1017	2.5
	14-11-2020	0845	Fine	0	0	0	20.9	23 / 1018	2.5
	14-11-2020	1345	Fine	0	0	0	20.9	23 / 1017	2.5
	14-11-2020	1645	Fine	0	0	0	20.9	23 / 1017	2.5

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		14-11-2020
Laboratory Staff:			
Checked by:	Chun Chun Au (Senior Foreman)		14-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-250C (GRAE II)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 415D	14/11/2020	0835	Fine	0	0	0	20.9	23 / 1018	2.5
	14/11/2020	0855	Fine	0	0	0	20.9	23 / 1017	2.8
CHFC 0740	14/11/2020	0940	Fine	0	0	0	20.9	23 / 1018	2.5
	14/11/2020	1420	Fine	0	0	0	20.9	23 / 1017	2.5
PAC	14/11/2020	2015	Fine	0	0	0	20.9	23 / 1018	2
	14/11/2020	1945	Fine	0	0	0	20.9	23 / 1017	2
PAC 2166	14/11/2020	2055	Fine	0	0	0	20.9	23 / 1018	2.1
	14/11/2020	1945	Fine	0	0	0	20.9	23 / 1017	2.1
137PAC	14/11/2020	0945	Fine	0	0	0	20.9	23 / 1018	1.4
	14/11/2020	1445	Fine	0	0	0	20.9	23 / 1017	1.4
137PAB	14/11/2020	0955	Fine	0	0	0	20.9	23 / 1018	1
	14/11/2020	1455	Fine	0	0	0	20.9	23 / 1017	1
WPR1	14/11/2020	1015	Fine	0	0	0	20.9	23 / 1018	0.6
	14/11/2020	1515	Fine	0	0	0	20.9	23 / 1017	0.6

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		14/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring --Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (GRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHA 6+70	14/11/2020	1525	Fine	0	0	0	20.9	23/1018	3.5
	14/11/2020	152x	Fine	0	0	0	20.9	23/1019	3.5
WPK 3	14/11/2020	1535	Fine	0	0	0	20.9	23/1018	4.2
	14/11/2020	1535	Fine	0	0	0	20.9	23/1019	4.2
Pit A	14/11/2020	1545	Fine	0	0	0	20.9	23/1018	2
	14/11/2020	1545	Fine	0	0	0	20.9	23/1019	2
Pit B	14/11/2020	1555	Fine	0	0	0	20.9	23/1018	8
	14/11/2020	1555	Fine	0	0	0	20.9	23/1019	8
								/	
								/	
								/	
								/	
								/	

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipa])		14/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PCM-2600 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	16-11-2020	0830	Fine	0	0	0	20.9	25 / 1019	2.5
	16-11-2020	1330	Fine	0	0	0	20.9	27 / 1016	2.5
	16-11-2020	1700	Fine	0	0	0	20.9	24 / 1016	2.5
Area B	16-11-2020	0845	Fine	0	0	0	20.9	25 / 1019	2.5
	16-11-2020	1345	Fine	0	0	0	20.9	27 / 1016	2.5
	16-11-2020	1645	Fine	0	0	0	20.9	24 / 1016	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		16-11-2020
Laboratory Staff:			
Checked by:	Chan yan tau (Senior Foreman)		16-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.PC4+S0	16/11/2020	0855	Fine	0	0	0	20.9	24/1014	2.5
	16/11/2020	1355	Fine	0	0	0	20.9	27/1016	2.5
CH.FC 0490	16/11/2020	0950	Fine	0	0	0	20.9	24/1014	2.5
	16/11/2020	1400	Fine	0	0	0	20.9	27/1016	2.5
Pit C	16/11/2020	0915	Fine	0	0	0	20.9	24/1014	2
	16/11/2020	1415	Fine	0	0	0	20.9	27/1016	2
137 CHC12+60	16/11/2020	0955	Fine	0	0	0	20.9	24/1014	2.1
	16/11/2020	1435	Fine	0	0	0	20.9	27/1016	2.1
137 Pit C	16/11/2020	0945	Fine	0	0	0	20.9	24/1014	1.4
	16/11/2020	1445	Fine	0	0	0	20.9	27/1016	1.4
137 Pit B	16/11/2020	0955	Fine	0	0	0	20.9	25/1014	2
	16/11/2020	1455	Fine	0	0	0	20.9	27/1016	2
137 Pit A	16/11/2020	1305	Fine	0	0	0	20.9	25/1014	2
	16/11/2020	1505	Fine	0	0	0	20.9	27/1016	2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		16/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR 1	16/11/2020	1015	Fine	0	0	0	20.9	25/1014	2.2
CHA 6+10	16/11/2020	1015	Fine	0	0	0	20.9	26/1016	2.2
	16/11/2020	1025	Fine	0	0	0	20.9	25/1019	3.5
WPR 3	16/11/2020	1025	Fine	0	0	0	20.9	25/1016	3.5
	16/11/2020	1035	Fine	0	0	0	20.9	25/1019	4.2
Pit A	16/11/2020	1035	Fine	0	0	0	20.9	25/1016	4.2
	16/11/2020	1045	Fine	0	0	0	20.9	25/1019	2
Pit B	16/11/2020	1045	Fine	0	0	0	20.9	25/1016	2
	16/11/2020	1055	Fine	0	0	0	20.9	25/1014	-8
	16/11/2020	1055	Fine	0	0	0	20.9	25/1016	2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		16/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28





Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	17-11-2020	0830	Fine	0	0	0	20.9	24/1017	2.5
	17-11-2020	1330	Fine	0	0	0	20.9	26/1018	2.5
	17-11-2020	1720	Fine	0	0	0	20.9	24/1018	2.5
Area B	17-11-2020	0845	Fine	0	0	0	20.9	24/1017	2.5
	17-11-2020	1345	Fine	0	0	0	20.9	26/1018	2.5
	17-11-2020	1645	Fine	0	0	0	20.9	24/1018	2.5

Name & Designation Signature Date
 Field Operator: Eric Man (Sub-Agent [RenoPipe])  17-11-2020
 Laboratory Staff:
 Checked by:  (Senior Foreman) 17-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Datos calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.FC 4+50	17/11/2020	0855	Fine	0	0	0	20.9	27/1017	2.5
	17/11/2020	1355	Fine	0	0	0	20.9	26/1015	2.5
CH.FC 0+90	17/11/2020	0920	Fine	0	0	0	20.9	27/1017	2.5
	17/11/2020	1425	Fine	0	0	0	20.9	25/1013	2.5
Pit C	17/11/2020	0915	Fine	0	0	0	20.9	23/1019	8
	17/11/2020	1415	Fine	0	0	0	20.9	23/1019	8
137 HCT 2tb	17/11/2020	0935	Fine	0	0	0	20.9	24/1017	3.1
	17/11/2020	1455	Fine	0	0	0	20.9	23/1015	3.1
137 Pit C	17/11/2020	0945	Fine	0	0	0	20.9	24/1017	1.4
	17/11/2020	1445	Fine	0	0	0	20.9	23/1015	1.4
137 Pit B	17/11/2020	0955	Fine	0	0	0	20.9	24/1017	2
	17/11/2020	1455	Fine	0	0	0	20.9	23/1015	2
137 Pit A	17/11/2020	1005	Fine	0	0	0	20.9	23/1017	2
	17/11/2020	1505	Fine	0	0	0	20.9	23/1015	2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RencPipe])		17/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	26 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPE 1	17/11/2020	1015	Fine	0	0	0	20.9	25/1017	2.2
CHA 6470	17/11/2020	1315	Fine	0	0	0	20.9	25/1015	2.2
	17/11/2020	1025	Fine	0	0	0	20.9	25/1017	3.5
WPE 3	17/11/2020	1525	Fine	0	0	0	20.9	25/1015	3.5
	17/11/2020	1035	Fine	0	0	0	20.9	25/1017	4.2
Pit A	17/11/2020	1535	Fine	0	0	0	20.9	25/1015	4.2
	17/11/2020	1045	Fine	0	0	0	20.9	25/1017	2
Pit B	17/11/2020	1545	Fine	0	0	0	20.9	25/1015	2
	17/11/2020	1055	Fine	0	0	0	20.9	25/1017	8

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		17/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28





Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	18-11-2020	0830	Fine	0	0	0	20.9	24/1015	2.5
	18-11-2020	1330	Fine	0	0	0	20.9	27/1016	2.5
	18-11-2020	1700	Fine	0	0	0	20.9	25/1011	2.5
Area B	18-11-2020	0845	Fine	0	0	0	20.9	24/1015	2.5
	18-11-2020	1345	Fine	0	0	0	20.9	27/1012	2.5
	18-11-2020	1645	Fine	0	0	0	20.9	25/1011	2.5

Name & Designation Signature Date
 Field Operator: Eric Man (Sub-Agent [RanoPipe])  18-11-2020
 Laboratory Staff:
 Checked by:  (Senior Foreman) 18-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location:	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.PC 4+50	18/11/2020	0835	Fine	0	0	0	26.4	28 / 1015	2.5
	18/11/2020	1355	Fine	0	0	0	26.4	29 / 1012	2.5
CH.PC 6+90	18/11/2020	0905	Fine	0	0	0	26.4	28 / 1015	2.5
	18/11/2020	1400	Fine	0	0	0	26.4	29 / 1012	2.5
Pit C	18/11/2020	0915	Fine	0	0	0	26.4	28 / 1015	8
	18/11/2020	1415	Fine	0	0	0	26.4	29 / 1011	8
157 (HC 2+16)	18/11/2020	0935	Fine	0	0	0	26.4	28 / 1015	3.1
	18/11/2020	1435	Fine	0	0	0	26.4	28 / 1011	3.1
157 Pit C	18/11/2020	0945	Fine	0	0	0	26.4	28 / 1015	1.4
	18/11/2020	1445	Fine	0	0	0	26.4	28 / 1011	1.4
157 Pit B	18/11/2020	0955	Fine	0	0	0	26.4	28 / 1015	2
	18/11/2020	1455	Fine	0	0	0	26.4	28 / 1011	2
157 Pit A	18/11/2020	1005	Fine	0	0	0	26.4	28 / 1015	2
	18/11/2020	1505	Fine	0	0	0	26.4	28 / 1011	2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		18/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PCM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR 1	18/11/2020	1015	Fine	0	0	0	20.9	28 / 1015	2.2
CHA 6+70	18/11/2020	1015	Fine	0	0	0	20.9	27 / 1011	2.2
	18/11/2020	1025	Fine	0	0	0	20.9	28 / 1015	3.5
WPR 3	18/11/2020	1025	Fine	0	0	0	20.9	29 / 1011	3.5
	18/11/2020	1035	Fine	0	0	0	20.9	28 / 1015	4.2
Pt A	18/11/2020	1045	Fine	0	0	0	20.9	27 / 1011	4.2
	18/11/2020	1045	Fine	0	0	0	20.9	26 / 1014	2
Pt B	18/11/2020	1055	Fine	0	0	0	20.9	27 / 1011	2
	18/11/2020	1055	Fine	0	0	0	20.9	26 / 1014	8

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		18/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PCM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	19-11-2020	0830	Fine	0	0	0	20.9	24/1013	2.5
	19-11-2020	1330	Fine	0	0	0	20.9	28/1011	2.5
	19-11-2020	1700	Fine	0	0	0	20.9	27/1010	2.5
Area B	19-11-2020	0845	Fine	0	0	0	20.9	24/1013	2.5
	19-11-2020	1345	Fine	0	0	0	20.9	28/1011	2.5
	19-11-2020	1645	Fine	0	0	0	20.9	27/1010	2.5

Name & Designation Signature Date
 Field Operator: Eric Man (Sub-Agent [RenoPipe]) 19-11-2020

Laboratory Staff:

Checked by: (Senior Foreman) Kwan 19-11-2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying In Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC430	19/11/2020	0820	Fine	0	0	0	20.9	24/1014	2.5
CHFC 0790	19/11/2020	1355	Fine	0	0	0	20.9	27/1210	2.5
	19/11/2020	0900	Fine	0	0	0	20.9	24/1014	2.2
Pit C	19/11/2020	1400	Fine	0	0	0	20.9	27/1010	2.5
	19/11/2020	0915	Fine	0	0	0	20.9	24/1014	2
157 HCT 2766	19/11/2020	1415	Fine	0	0	0	20.9	27/1010	2
	19/11/2020	0935	Fine	0	0	0	20.9	25/1014	3.1
157 Pit C	19/11/2020	1435	Fine	0	0	0	20.9	28/1010	3.1
	19/11/2020	0945	Fine	0	0	0	20.9	25/1014	1.4
157 Pit B	19/11/2020	1445	Fine	0	0	0	20.9	28/1010	1.4
	19/11/2020	0955	Fine	0	0	0	20.9	25/1014	2
157 Pit A	19/11/2020	1455	Fine	0	0	0	20.9	28/1010	2
	19/11/2020	1005	Fine	0	0	0	20.9	25/1014	2
	19/11/2020	1505	Fine	0	0	0	20.9	28/1010	2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		19/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR 1	19/11/2020	1015	Fine	0	0	0	20.9	25 / 1014	2.2
CHA 6+70	19/11/2020	1515	Fine	0	0	0	20.9	28 / 1010	2.2
	19/11/2020	1025	Fine	0	0	0	20.9	25 / 1014	3.5
WPR 3	19/11/2020	1525	Fine	0	0	0	20.9	28 / 1010	3.5
	19/11/2020	1035	Fine	0	0	0	20.9	25 / 1014	4.2
Pit A	19/11/2020	1535	Fine	0	0	0	20.9	28 / 1010	4.2
	19/11/2020	1045	Fine	0	0	0	20.9	25 / 1013	2
Pit B	19/11/2020	1545	Fine	0	0	0	20.9	28 / 1010	2
	19/11/2020	1055	Fine	0	0	0	20.9	25 / 1013	8
	19/11/2020	1555	Fine	0	0	0	20.9	28 / 1010	8

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		19/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used: PGM-2500 (QRAE III)	Dates calibrated: 28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	20-11-2020	0830	Fine	0	0	0	20.9	25 / 1014	2.5
	20-11-2020	1330	Fine	0	0	0	20.9	29 / 1011	2.5
	20-11-2020	1708	Fine	0	0	0	20.9	26 / 1011	2.5
Area B	20-11-2020	0840	Fine	0	0	0	20.9	25 / 1014	2.5
	20-11-2020	1414	Fine	0	0	0	20.9	29 / 1011	2.5
	20-11-2020	1648	Fine	0	0	0	20.9	26 / 1011	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		20-11-2020
Laboratory Staff:			
Checked by:	Chan Yan-tau (Senior Foreman) 20-11-2020		

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 0450	20/11/2020	0855	Fine	0	0	0	20.9	25/1014	2.3
	20/11/2020	1355	Fine	0	0	0	20.9	23/1011	2.3
CHFC 0490	20/11/2020	0930	Fine	0	0	0	20.9	25/1014	2.5
	20/11/2020	1430	Fine	0	0	0	20.9	23/1011	2.5
Pit C	20/11/2020	0915	Fine	0	0	0	20.9	25/1014	8
	20/11/2020	1415	Fine	0	0	0	20.9	23/1011	8
137CHC0460	20/11/2020	0935	Fine	0	0	0	20.9	26/1014	3.1
	20/11/2020	1435	Fine	0	0	0	20.9	23/1011	3.1
137 Pit C	20/11/2020	0945	Fine	0	0	0	20.9	26/1014	1.4
	20/11/2020	1445	Fine	0	0	0	20.9	23/1011	1.4
137 Pit B	20/11/2020	0955	Fine	0	0	0	20.9	26/1014	2
	20/11/2020	1455	Fine	0	0	0	20.9	23/1011	2
137 Pit A	20/11/2020	1005	Fine	0	0	0	20.9	26/1014	2
	20/11/2020	1505	Fine	0	0	0	20.9	23/1011	2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		20/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring – Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR 1	28/11/2020	1015	Fine	0	0	0	20.9	26 / 1014	2.2
	28/11/2020	1315	Fine	0	0	0	20.9	28 / 1011	2.2
CHA 6+7a	28/11/2020	1225	Fine	0	0	0	20.9	27 / 1014	3.5
	28/11/2020	1325	Fine	0	0	0	20.9	28 / 1011	3.5
WPR 3	28/11/2020	1235	Fine	0	0	0	20.9	27 / 1014	4.2
	28/11/2020	1335	Fine	0	0	0	20.9	28 / 1011	4.2
Pit A	28/11/2020	1045	Fine	0	0	0	20.9	27 / 1013	2
	28/11/2020	1345	Fine	0	0	0	20.9	28 / 1011	2
Pit B	28/11/2020	1055	Fine	0	0	0	20.9	27 / 1013	8
	28/11/2020	1355	Fine	0	0	0	20.9	28 / 1011	8

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		28/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring -Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	21-11-2020	0830	Fine	0	0	0	20.9	22/1016	2.5
	21-11-2020	1330	Fine	0	0	0	20.9	23/1014	2.5
	21-11-2020	1700	Fine	0	0	0	20.9	23/1014	2.5
Area B	21-11-2020	0845	Fine	0	0	0	20.9	22/1016	2.5
	21-11-2020	1345	Fine	0	0	0	20.9	23/1014	2.5
	21-11-2020	1645	Fine	0	0	0	20.9	23/1014	2.5

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent (RenoPipe))		21-11-2020
Laboratory Staff:			
Checked by:	Chengyan Cao (Senior Foreman) Cao 21-11-2020		

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mba)	Remark Depth (m)
CH.FE 4+50	21/11/2020	0858	Fine	0	0	0	20.9	22/1016	2.5
CH.FE 4+50	21/11/2020	1358	Fine	0	0	0	20.9	23/1016	2.5
CH.FE 4+50	21/11/2020	0900	Fine	0	0	0	20.9	22/1016	2.5
pit C	21/11/2020	1200	Fine	0	0	0	20.9	23/1016	2.5
pit C	21/11/2020	0935	Fine	0	0	0	20.9	22/1016	2
137 CH.T 2+00	21/11/2020	1418	Fine	0	0	0	20.9	23/1016	2
137 CH.T 2+00	21/11/2020	0935	Fine	0	0	0	20.9	22/1016	2.1
137 pit C	21/11/2020	1435	Fine	0	0	0	20.9	23/1016	2.1
137 pit C	21/11/2020	0945	Fine	0	0	0	20.9	22/1016	1.4
137 pit B	21/11/2020	1445	Fine	0	0	0	20.9	23/1016	1.4
137 pit B	21/11/2020	0955	Fine	0	0	0	20.9	22/1016	2
137 pit A	21/11/2020	1455	Fine	0	0	0	20.9	23/1016	2
137 pit A	21/11/2020	1005	Fine	0	0	0	20.9	22/1016	2
137 pit A	21/11/2020	1508	Fine	0	0	0	20.9	23/1016	2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		21/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28




Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPK 1	21/11/2020	1015	Fine	0	0	0	20.9	22 / 1016	2.2
CHA 670	21/11/2020	1515	Fine	0	0	0	20.9	23 / 1014	2.2
	21/11/2020	1025	Fine	0	0	0	20.9	22 / 1016	3.5
WPK 3	21/11/2020	1525	Fine	0	0	0	20.9	23 / 1014	3.5
	21/11/2020	1035	Fine	0	0	0	20.9	22 / 1016	4.2
Pit A	21/11/2020	1535	Fine	0	0	0	20.9	23 / 1014	4.2
	21/11/2020	1045	Fine	0	0	0	20.9	22 / 1016	2
Pit B	21/11/2020	1545	Fine	0	0	0	20.9	23 / 1014	2
	21/11/2020	1055	Fine	0	0	0	20.9	22 / 1016	8
	21/11/2020	1555	Fine	0	0	0	20.9	23 / 1014	8

Name & Designation Signature Date
 Field Operator: Eric Man (Sub-Agent [RenoPipe])  21/11/2020
 Laboratory Staff:
 Checked by:

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	23-11-2020	0830	Fine	0	0	0	20.9	22/1021	2.5
	23-11-2020	1330	Fine	0	0	0	20.9	22/1019	2.5
	23-11-2020	1700	Fine	0	0	0	20.9	22/1019	2.5
Area B	23-11-2020	0845	Fine	0	0	0	20.9	22/1021	2.5
	23-11-2020	1545	Fine	0	0	0	20.9	22/1019	2.5
	23-11-2020	1645	Fine	0	0	0	20.9	22/1019	2.5

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		23-11-2020
Laboratory Staff:			
Checked by:	Chau Chi Fai (Foreman) 23/11/2020		

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring -Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	26 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.FC 4+30	23/11/2020	0825	Fine	0	0	0	20.9	22/1021	2.5
	23/11/2020	1335	Fine	0	0	0	20.9	22/1019	2.5
CH.FC 0+90	23/11/2020	0900	Fine	0	0	0	20.9	22/1021	2.5
	23/11/2020	1400	Fine	0	0	0	20.9	22/1019	2.5
Pit C	23/11/2020	0915	Fine	0	0	0	20.9	22/1021	8
	23/11/2020	1415	Fine	0	0	0	20.9	22/1019	8
137(HCT 2+66	23/11/2020	0935	Fine	0	0	0	20.9	22/1021	3.1
	23/11/2020	1435	Fine	0	0	0	20.9	22/1019	3.1
137 Pit C	23/11/2020	0945	Fine	0	0	0	20.9	22/1021	1.4
	23/11/2020	1445	Fine	0	0	0	20.9	22/1019	1.4
137 Pit B	23/11/2020	0955	Fine	0	0	0	20.9	22/1021	2
	23/11/2020	1455	Fine	0	0	0	20.9	22/1019	2
137 Pit A	23/11/2020	1005	Fine	0	0	0	20.9	22/1021	2
	23/11/2020	1505	Fine	0	0	0	20.9	22/1019	2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		23/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	26 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR 1	23/11/2020	1015	Fine	0	0	0	20.9	22/1021	2.2
	23/11/2020	1315	Fine	0	0	0	20.9	22/1019	2.2
CHA 6770	23/11/2020	1025	Fine	0	0	0	20.9	22/1021	3.5
	23/11/2020	1325	Fine	0	0	0	20.9	22/1019	3.5
WPR 3	23/11/2020	1035	Fine	0	0	0	20.9	22/1021	4.2
	23/11/2020	1335	Fine	0	0	0	20.9	22/1019	4.2
Pit A	23/11/2020	1045	Fine	0	0	0	20.9	22/1021	2
	23/11/2020	1345	Fine	0	0	0	20.9	22/1019	2
Pit B	23/11/2020	1055	Fine	0	0	0	20.9	22/1021	8
	23/11/2020	1355	Fine	0	0	0	20.9	22/1019	8

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		23/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28




Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mba-)	Remark Depth (m)
Area A	24-11-2020	0830	Fine	0	0	0	20.9	23 / 1021	2.5
	24-11-2020	1330	Fine	0	0	0	20.9	25 / 1018	2.5
	24-11-2020	1700	Fine	0	0	0	20.9	22 / 1018	2.5
Area B	24-11-2020	0845	Fine	0	0	0	20.9	23 / 1021	2.5
	24-11-2020	1345	Fine	0	0	0	20.9	25 / 1018	2.5
	24-11-2020	1645	Fine	0	0	0	20.9	22 / 1018	2.5

Field Operator: Eric Man (Sub-Agent [RenoPipe])  Date: 24-11-2020

Laboratory Staff:

Checked by:  Date: 24/11/2020

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.FC 4+30	24/11/2020	0855	Fine	0	0	0	20.9	23 / 1021	2.5
	24/11/2020	1355	Fine	0	0	0	20.9	24 / 1018	2.5
CH.FC 0+40	24/11/2020	0900	Fine	0	0	0	20.9	23 / 1021	2.5
	24/11/2020	1430	Fine	0	0	0	20.9	24 / 1017	2.5
P+C	24/11/2020	0915	Fine	0	0	0	20.9	23 / 1021	2
	24/11/2020	1415	Fine	0	0	0	20.9	24 / 1017	2
137CHCT2+6	24/11/2020	0935	Fine	0	0	0	20.9	23 / 1021	2.1
	24/11/2020	1435	Fine	0	0	0	20.9	24 / 1017	2.1
137 P+C	24/11/2020	0945	Fine	0	0	0	20.9	24 / 1021	2
	24/11/2020	1445	Fine	0	0	0	20.9	23 / 1017	2
137 P+B	24/11/2020	0955	Fine	0	0	0	20.9	24 / 1021	2
	24/11/2020	1455	Fine	0	0	0	20.9	23 / 1017	2
137 P+A	24/11/2020	1005	Fine	0	0	0	20.9	24 / 1020	2
	24/11/2020	1505	Fine	0	0	0	20.9	23 / 1017	2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent (RenoPipe))		24/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPK 1	24/11/2020	1018	Fine	0	0	0	20.9	24/1020	2.2
	24/11/2020	1518	Fine	0	0	0	20.9	24/1019	2.2
CHA 6+70	24/11/2020	1025	Fine	0	0	0	20.9	25/1020	3.5
	24/11/2020	1525	Fine	0	0	0	20.9	25/1019	3.5
WPK 3	24/11/2020	1032	Fine	0	0	0	20.9	25/1020	4.2
	24/11/2020	1532	Fine	0	0	0	20.9	22/1017	4.2
P+A	24/11/2020	1045	Fine	0	0	0	20.9	25/1020	2
	24/11/2020	1545	Fine	0	0	0	20.9	22/1017	2
P+B	24/11/2020	1055	Fine	0	0	0	20.9	25/1020	8
	24/11/2020	1555	Fine	0	0	0	20.9	22/1018	8

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent (RenoPipe))		24/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	28-11-2020	0830	Fine	0	0	0	20.9	22 / 1019	4.2
	28-11-2020	1330	Fine	0	0	0	20.9	21 / 1017	4.2
	28-11-2020	1700	Fine	0	0	0	20.9	21 / 1017	4.2
Area B	28-11-2020	0845	Fine	0	0	0	20.9	22 / 1019	2.5
	28-11-2020	1345	Fine	0	0	0	20.9	21 / 1017	2.5
	28-11-2020	1645	Fine	0	0	0	20.9	21 / 1017	2.5

Field Operator: Eric Man (Sub-Agent (RenoPipe)) *[Signature]* 28-11-2020

Laboratory Staff:

Checked by: *Chau Chi Fai* (Foam) 28/11/2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PCM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.Fc 4X0	25/11/2020	0855	Fine	0	0	0	20.9	22/1020	2.5
	25/11/2020	1555	Fine	0	0	0	20.9	27/1017	2.5
CH.Fc 0790	25/11/2020	0900	Fine	0	0	0	20.9	22/1020	2.5
	25/11/2020	1400	Fine	0	0	0	20.9	27/1017	2.5
Pit C	25/11/2020	0915	Fine	0	0	0	20.9	22/1020	2
	25/11/2020	1415	Fine	0	0	0	20.9	27/1017	2
137 PACT 2+6b	25/11/2020	0935	Fine	0	0	0	20.9	23/1020	3.1
	25/11/2020	1435	Fine	0	0	0	20.9	27/1017	3.1
137 Pit C	25/11/2020	0945	Fine	0	0	0	20.9	23/1020	1.4
	25/11/2020	1445	Fine	0	0	0	20.9	27/1017	1.4
137 Pit B	25/11/2020	0955	Fine	0	0	0	20.9	25/1020	2
	25/11/2020	1455	Fine	0	0	0	20.9	27/1017	2
137 Pit A	25/11/2020	1005	Fine	0	0	0	20.9	24/1020	2
	25/11/2020	1505	Fine	0	0	0	20.9	27/1017	2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		25/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28




Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
FGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPK 1	25/11/2020	1015	Fine	0	0	0	20.9	24/1020	2.2
CHA 6+10	25/11/2020	1315	Fine	0	0	0	20.9	27/1017	2.2
	25/11/2020	1025	Fine	0	0	0	20.9	24/1020	3.5
WPK 5	25/11/2020	1525	Fine	0	0	0	20.9	27/1016	3.5
	25/11/2020	1035	Fine	0	0	0	20.9	24/1020	4.2
Pit A	25/11/2020	1335	Fine	0	0	0	20.9	27/1016	4.2
	25/11/2020	1045	Fine	0	0	0	20.9	24/1020	2
Pit B	25/11/2020	1545	Fine	0	0	0	20.9	27/1016	2
	25/11/2020	1055	Fine	0	0	0	20.9	24/1020	2
	25/11/2020	1555	Fine	0	0	0	20.9	27/1016	2
								/	
								/	
								/	

Name & Designation Signature Date
 Field Operator: Eric Man (Sub-Agent [RenoPipe])  25/11/2020
 Laboratory Staff:
 Checked by:

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	26-11-2020	0830	Fine	0	0	0	20.9	12/1021	4.2
	26-11-2020	1330	Fine	0	0	0	20.9	28/1017	4.2
	26-11-2020	1700	Fine	0	0	0	20.9	26/1017	4.2
Area B	26-11-2020	0845	Fine	0	0	0	20.9	22/1021	2.5
	26-11-2020	1345	Fine	0	0	0	20.9	28/1017	2.5
	26-11-2020	1645	Fine	0	0	0	20.9	26/1017	2.5
							/		
							/		
							/		
							/		
							/		
							/		
							/		

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		26-11-2020
Laboratory Staff:			
Checked by:	Chau Ke Fai (Foreman)		28/11/2020

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
FGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4+5	26/11/2020	0855	Fine	0	0	0	20.9	29 / 1021	2.5
	26/11/2020	1555	Fine	0	0	0	20.9	28 / 1019	2.5
CHFC 0+1C	26/11/2020	0900	Fine	0	0	0	20.9	29 / 1021	2.5
	26/11/2020	1400	Fine	0	0	0	20.9	28 / 1019	2.5
Pit C	26/11/2020	0915	Fine	0	0	0	20.9	29 / 1021	2
	26/11/2020	1415	Fine	0	0	0	20.9	27 / 1019	2
137 CHC 2+6b	26/11/2020	0935	Fine	0	0	0	20.9	24 / 1021	3.1
	26/11/2020	1435	Fine	0	0	0	20.9	27 / 1019	3.1
137 Pit C	26/11/2020	0945	Fine	0	0	0	20.9	24 / 1021	1.4
	26/11/2020	1445	Fine	0	0	0	20.9	27 / 1019	1.4
137 Pit B	26/11/2020	0955	Fine	0	0	0	20.9	24 / 1021	2
	26/11/2020	1455	Fine	0	0	0	20.9	27 / 1019	2
137 Pit A	26/11/2020	1005	Fine	0	0	0	20.9	24 / 1021	2
	26/11/2020	1505	Fine	0	0	0	20.9	27 / 1019	2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		26/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring - Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-250C (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR 1	26/11/2020	1015	Fine	0	0	0	20.9	25/1021	2.2
	26/11/2020	1515	Fine	0	0	0	20.9	27/1017	2.2
CHA 6+70	26/11/2020	1025	Fine	0	0	0	20.9	25/1021	3.5
	26/11/2020	1525	Fine	0	0	0	20.9	27/1017	3.5
WPR 3	26/11/2020	1055	Fine	0	0	0	20.9	25/1021	4.2
	26/11/2020	1535	Fine	0	0	0	20.9	27/1017	4.2
Pit A	26/11/2020	1045	Fine	0	0	0	20.9	25/1021	2
	26/11/2020	1545	Fine	0	0	0	20.9	27/1017	2
Pit B	26/11/2020	1055	Fine	0	0	0	20.9	25/1021	8
	26/11/2020	1555	Fine	0	0	0	20.9	27/1017	8

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		26/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28




Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet


Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-250C (QRAE II)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	27-11-2020	0830	Fine	0	0	0	20.9	21/1022	4.2
	27-11-2020	1330	Fine	0	0	0	20.9	25/1019	4.2
	27-11-2020	1700	Fine	0	0	0	20.9	24/1019	4.2
Area B	27-11-2020	0845	Fine	0	0	0	20.9	21/1022	2.5
	27-11-2020	1345	Fine	0	0	0	20.9	25/1019	2.5
	27-11-2020	1645	Fine	0	0	0	20.9	24/1019	2.5

Field Operator: Eric Man (Sub-Agent [RenoPipe])  27-11-2020

Laboratory Staff:

Checked by:  27/11/2020

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4+30	27/11/2020	0835	Fine	0	0	0	20.6	22/1022	2.5
	27/11/2020	1335	Fine	0	0	0	20.9	25/1019	2.5
CHFC 4+40	27/11/2020	0900	Fine	0	0	0	20.6	27/1024	2.5
	27/11/2020	1400	Fine	0	0	0	20.3	25/1029	2.5
Pit C	27/11/2020	0915	Fine	0	0	0	20.3	22/1022	3
	27/11/2020	1415	Fine	0	0	0	20.3	25/1018	3
137 CHRT 2+66	27/11/2020	0935	Fine	0	0	0	20.9	22/1023	3.1
	27/11/2020	1435	Fine	0	0	0	20.6	25/1018	3.1
137 Pit C	27/11/2020	0945	Fine	0	0	0	20.9	22/1023	1.4
	27/11/2020	1445	Fine	0	0	0	20.9	25/1018	1.4
137 Pit B	27/11/2020	0955	Fine	0	0	0	20.9	22/1023	2
	27/11/2020	1455	Fine	0	0	0	20.9	25/1018	2
137 Pit A	27/11/2020	1005	Fine	0	0	0	20.9	25/1022	2
	27/11/2020	1505	Fine	0	0	0	20.9	25/1018	2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent (RenoPipe))		27/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (GRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPK 1	27/11/2020	1015	Fine	0	0	0	20.9	23/1022	2.2
	27/11/2020	1315	Fine	0	0	0	20.9	25/1018	2.2
CHA 676	27/11/2020	1025	Fine	0	0	0	20.9	25/1022	3.5
	27/11/2020	1525	Fine	0	0	0	20.9	25/1018	3.5
WPK 3	27/11/2020	1035	Fine	0	0	0	20.9	23/1022	4.2
	27/11/2020	1335	Fine	0	0	0	20.9	25/1018	4.2
Pit A	27/11/2020	1045	Fine	0	0	0	20.9	23/1022	2
	27/11/2020	1845	Fine	0	0	0	20.9	25/1018	2
Pit B	27/11/2020	1055	Fine	0	0	0	20.9	23/1022	8
	27/11/2020	1555	Fine	0	0	0	20.9	25/1018	8
								/	
								/	
								/	
								/	

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent (RenoPipe))		27/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-250C (QRAE II)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	28-11-2020	0830	Fine	0	0	0	20.9	18 / 102.4	4.2
	28-11-2020	1330	Fine	0	0	0	20.9	22 / 102.1	4.2
	28-11-2020	1700	Fine	0	0	0	20.9	20 / 102.1	4.2
Area B	28-11-2020	0845	Fine	0	0	0	20.9	18 / 102.3	2.5
	28-11-2020	1345	Fine	0	0	0	20.9	22 / 102.1	2.5
	28-11-2020	1645	Fine	0	0	0	20.9	20 / 102.1	2.5
							/		
							/		
							/		
							/		
							/		
							/		
							/		

Name & Designation Signature Date

Field Operator: Eric Man (Sub-Agent [RenoPipe]) 28-11-2020

Laboratory Staff:

Checked by: 28/11/2020

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4+50	28/11/2020	0835	Fine	0	0	0	20.9	18 / 1024	2.5
	28/11/2020	0955	Fine	0	0	0	20.9	21 / 1021	2.5
CH.FC 0+90	28/11/2020	0900	Fine	0	0	0	20.9	18 / 1024	2.5
	28/11/2020	1400	Fine	0	0	0	20.9	21 / 1021	2.5
Pit C	28/11/2020	0915	Fine	0	0	0	20.9	18 / 1024	8
	28/11/2020	1415	Fine	0	0	0	20.9	21 / 1021	8
P57CHCT2+66	28/11/2020	0955	Fine	0	0	0	20.9	19 / 1024	3.1
	28/11/2020	1435	Fine	0	0	0	20.9	21 / 1020	3.1
137 Pit C	28/11/2020	0945	Fine	0	0	0	20.9	19 / 1024	1.4
	28/11/2020	1445	Fine	0	0	0	20.9	21 / 1020	1.4
137 Pit B	28/11/2020	0955	Fine	0	0	0	20.9	19 / 1024	2
	28/11/2020	1455	Fine	0	0	0	20.9	21 / 1020	2
137 Pit A	28/11/2020	1005	Fine	0	0	0	20.9	19 / 1024	2
	28/11/2020	1805	Fine	0	0	0	20.9	21 / 1020	2

	<u>Name & Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		28/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring --Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE II)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR1	28/11/2020	1015	Fine	0	0	0	20.9	19 / 1024	2.2
CHA 670	28/11/2020	1515	Fine	0	0	0	20.9	21 / 1020	2.2
	28/11/2020	1605	Fine	0	0	0	20.9	19 / 1024	2.5
WPR3	28/11/2020	1535	Fine	0	0	0	20.9	21 / 1020	2.5
	28/11/2020	1635	Fine	0	0	0	20.9	19 / 1024	4.2
Pit A	28/11/2020	1535	Fine	0	0	0	20.9	21 / 1020	4.2
	28/11/2020	1645	Fine	0	0	0	20.9	19 / 1024	2
Pit B	28/11/2020	1645	Fine	0	0	0	20.9	21 / 1020	2
	28/11/2020	1655	Fine	0	0	0	20.9	19 / 1024	3

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		28/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	30-11-2020	0830	Fine	0	0	0	20.9	16/1024	4.2
	30-11-2020	1330	Fine	0	0	0	20.9	22/1021	4.2
	30-11-2020	1700	Fine	0	0	0	20.9	21/1021	4.2
Area B	30-11-2020	0845	Fine	0	0	0	20.9	16/1024	2.5
	30-11-2020	1345	Fine	0	0	0	20.9	22/1021	2.5
	30-11-2020	1645	Fine	0	0	0	20.9	21/1021	2.5

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		30-11-2020
Laboratory Staff:			
Checked by:	Chan Ho Fai (Foreman)		30-11-2020

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4+50	30/11/2020	0835	Fine	0	0	0	20.9	16/1024	2.5
	30/11/2020	1355	Fine	0	0	0	20.9	21/1024	2.5
CHFC 6+90	30/11/2020	0900	Fine	0	0	0	20.9	16/1024	2.5
	30/11/2020	1400	Fine	0	0	0	20.9	21/1021	2.5
P+ C	30/11/2020	0910	Fine	0	0	0	20.9	16/1024	2
	30/11/2020	1415	Fine	0	0	0	20.9	21/1024	2
137 HCT2+66	30/11/2020	0935	Fine	0	0	0	20.9	17/1024	3.1
	30/11/2020	1435	Fine	0	0	0	20.9	22/1021	3.1
137 P+ C	30/11/2020	0945	Fine	0	0	0	20.9	17/1024	1.4
	30/11/2020	1445	Fine	0	0	0	20.9	22/1021	1.4
137 P+B	30/11/2020	0955	Fine	0	0	0	20.9	17/1024	2
	30/11/2020	1455	Fine	0	0	0	20.9	22/1021	2
137 P+A	30/11/2020	1005	Fine	0	0	0	20.9	17/1024	2
	30/11/2020	1505	Fine	0	0	0	20.9	22/1021	2

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent (RenoPipe))		30/11/2020
Laboratory Staff:			
Checked by:			

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28




Contract no. 13/WSD/16
 Mainlaying in Tseung Kwan O
 Penta-Ocean - Concentric Joint Venture
Landfill Gas Monitoring –Field Measurement Recording Sheet

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition:	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPK 1	30/11/2020	015	Fine	0	0	0	20.6	17/1024	2.2
	30/11/2020	1815	Fine	0	0	0	20.9	22/1021	2.2
CHA 6A10	30/11/2020	1025	Fine	0	0	0	20.9	17/1024	0.6
	30/11/2020	1525	Fine	0	0	0	20.9	22/1021	0.6
WPK 3	30/11/2020	1030	Fine	0	0	0	20.9	17/1024	4.2
	30/11/2020	1535	Fine	0	0	0	20.9	22/1021	4.2
Pit A	30/11/2020	1045	Fine	0	0	0	20.9	18/1024	2
	30/11/2020	1545	Fine	0	0	0	20.9	22/1021	2
Pit B	30/11/2020	1055	Fine	0	0	0	20.9	13/1024	8
	30/11/2020	1555	Fine	0	0	0	20.9	22/1021	8

Name & Designation Signature Date
 Field Operator: Eric Man (Sub-Agent [RenoPipe])  30/11/2020
 Laboratory Staff:
 Checked by:

Appendix K

Complaint Log and Regulatory Compliance Proforma

Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
01 November 2020 - 30 November 2020	1	1	EPD received a complaint from a member of the public with concern on construction noise associated with the captioned construction site. It was suspected that powered mechanical equipment such as roller and dump truck was used for the purpose of carrying out construction works on 15 November 2020 (Sunday).

Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Details
01 November 2020 - 30 November 2020	0	0	N/A

Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Details
01 November 2020 - 30 November 2020	0	0	N/A

Appendix L

Site Inspection Proforma



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 T: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

WEEKLY ENVIRONMENTAL INSPECTION CHECKLIST

Inspection Date: 03/11/2020 Inspected by: ET: Charlene Lai WSD: Tsang Kin Fai
 Contractor: Tim Chung Chu IEC: N/A

Inspection Time: 09:32 - 11:00

Weather Condition	<input type="checkbox"/> Sunny	<input type="checkbox"/> Fine	<input checked="" type="checkbox"/> Overcast	<input type="checkbox"/> Drizzle	<input type="checkbox"/> Rain	<input type="checkbox"/> Storm	<input type="checkbox"/> Hazy
Temperature	<input type="text" value="28"/> C		Humidity	<input checked="" type="checkbox"/> High	<input type="checkbox"/> Moderate	<input type="checkbox"/> Low	
Wind	<input type="checkbox"/> Calm	<input checked="" type="checkbox"/> Light	<input type="checkbox"/> Freeze	<input type="checkbox"/> Strong			

	N/A	Yes	No	Photo/Remarks
0.00 General				
0.01 Is the current Environmental Permit displayed conspicuously at all vehicle site entrances/exits for public's information at any time?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
0.02 Is ET Leader's log-book kept readily available for inspections?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.00 Construction Dust				
1.01 Are dusty materials, such as excavated materials, building debris and construction materials, and exposed earth surface properly covered to prevent dust emission?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>Obs (2)</u>
1.02 Are screenings, enclosures, water spraying or vacuum cleaning devices provided to dusty construction works for dust suppression?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>screening</u>
1.03 Are fumes or smoke emitting plants or construction activities shielded by a screen?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04 Are wheel-washing facilities with high-pressure water jets provided at all site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05 Is wheel-washing provided to all vehicles leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06 Are road section near the site exit free from dusty material?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.07 Are all main haul roads inside the site paved or sprayed with water to minimize dust emission during vehicle movement?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>paved</u>
1.08 Are water spraying provided immediately prior to any loading or transfer of dusty materials?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.09 Are covers provided to all dump trucks carrying dusty materials when entering and leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>No dump trucks observed</u>
1.10 Are the working areas for uprooting of trees, shrubs, or vegetation or the removal of boulders, poles, pillars sprayed with water to maintain the entire surface wet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11 Is exposed earth properly treated within six months after the last construction activity on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.12 Does the operation of plants on site free from dark smoke emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>✓NRMM (obs) Obs (1)</u>

03/11



Acuity Sustainability Consulting Limited
 Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
1.13	Are vehicles travelling at speed not exceeding 15km/hr within the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.14	Are stock of more than 20 bags of cement or dry PFA covered or sheltered on top and 3 sides?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.15	Are de-bagging, batching and mixing processes of bagged cement carried out in sheltered areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are hoarding of at least 2.4m high provided along the site boundary adjoining areas accessible by the public?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Is open burning prohibited?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.00	Construction Noise (Airborne)				
2.01	Are quiet plants adopted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.02	Are the PMEs operating on site well-maintained to minimize the generation of excessive noise?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.03	Are plants throttled down or turned off when not in use?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.04	Are the plants known to emit noise strongly in one direction oriented to face away from NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>No noise marks to the adjacent sites</i>
2.05	Are moveable barriers provided to screen NSRs from plant or noisy operations?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.06	Are silencers, mufflers and enclosures provided to plants?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Are the hoods, cover panels and inspection hatches of PMIs closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.08	Are purposely-built site hoarding construction with appropriate materials provided along the site boundary?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Are noisy operation properly scheduled to minimize exposure and cumulative impacts to nearby sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are valid noise emission label(s) affixed to all hand-held breakers operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Are valid noise emission label(s) affixed to all air compressors operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are all construction noise permit(s) applied for percussive piling work?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are construction noise permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are valid construction noise permit(s) displayed at all vehicular exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.00	Water Quality				
3.01	Is effluent discharge license obtained for wastewater discharge from site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.02	Is effluent discharged according to the effluent discharge license?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>No water was discharged on the reporting day.</i>
3.03	Is wastewater discharge from site properly treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

03/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
3.04	Are perimeter channels provided to intercept storm runoff from outside the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.05	Are sand/silt removal facilities such as sand/silt traps and sediment basins provided to remove sand/silt particles from runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.06	Is surface runoff diverted to sedimentation facilities?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.07	Is the drainage system properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.08	Are construction works carefully programmed to minimize soil excavation works during rainy seasons?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.09	Are exposed soil surface protected by paving as soon as possible to reduce the potential of soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Are temporary access roads protected by crushed gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.11	Are exposed slope surface properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Is trench excavation avoided in the wet season as far as practicable, or if necessary, backfilled in short sections after excavation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.13	Are open stockpiles of construction materials on site covered by tarpaulin or similar fabric during construction?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.14	Is runoff from wheel-washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.15	Is oil leakage or spillage prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.16	Are there any measures to prevent the release of oil and grease into the storm drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.17	Are the oil interceptors/ grease traps properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.18	Are debris and rubbish generated on site collected, handled and disposed of properly to avoid them entering the streams?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.19	Are all fuel tanks and storage areas provided with locks and be sited on sealed areas, within bunds of capacity equal to 110% of the storage capacity of the largest tank?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.20	Are tanks, containers, storage area bunded and the locations locked as far as possible from the sensitive watercourse and stormwater drains?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.21	Are sufficient chemical toilets provided on site to handle sewage from construction work force?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.22	Are sewage disposal and toilet maintenance of the portable chemical toilets provided by the licensed contractors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.23	Is concrete washing water properly collected and treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.00	Waste Management				
4.01	Is a trip-ticket system implemented to monitor the disposal of C&D and solid wastes at public filling facilities and landfills?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

03/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
4.02	Is a recording system implemented to record the amount of wastes generated, recycled and disposed of?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.03	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.04	Are chemical waste separated from other waste and collected by a licensed chemical waste collector?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Are trip tickets for chemical waste disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Is chemical waste reused and recycled on site as far as practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are all containers for chemical waste properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.08	Is chemical waste storage area used solely for storage of chemical waste and properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.09	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Is the chemical waste storage area enclosed on at least 3 sides and adequately ventilated?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.11	Is an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or of 20% by volume of the chemical waste stored in that area, whichever is the greatest, provide?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Are a routine cleaning and maintenance programme implemented for drainage systems, sump pits, and oil interceptors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Are sufficient general refuse disposal/collection points provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.15	Are appropriate measures adopted to minimize windblown litter and dust during transportation of waste?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.16	Are individual collectors for aluminum cans, plastic bottles and packaging material and office paper provided to encourage waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.17	Are C&D wastes sorted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.18	Are C&D waste disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.19	Are unused C&D materials or chemicals recycled or reused to reduce the quantity of waste?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are public fill and C&D waste reuse on site as far as practicable to avoid disposal off-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.21	Are the construction materials stored properly to minimize the potential for damage or contamination?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.22	Is a dumping license obtained to deliver public fill to public filling areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

03/11

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
5.00	Landscape and Visual				
5.01	Are site hoarding provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Are vegetation disturbance minimized or soil protected to reduce potential soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.03	Is construction light oriented away from the sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is grass hydroseeding provided to slopes as soon as the completion of works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Are damages to trees outside site boundary due construction works avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.06	Is excavation works carried out manually instead of machinery operation within 2.5m vicinity of any preserved trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.07	Are the retained and transplanted tree(s) properly protected and in good conditions?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.08	Are surgery works carried out for damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.00	Ecology				
6.01	Is site runoff properly treated to prevent any silty runoff?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	NO water was discharged
6.02	Are silt trap installed and well-maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.03	Are stockpiles properly covered to avoid generating silty runoff?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	obs (2)
6.04	Are construction works restricted to works area which are clearly defined?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7.00	Overall				
7.01	Is the EM&A properly implemented in general?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

03/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

Remark / Follow up of Observation(s) and Non-compliance(s) of Last Weekly Site Inspection:




Observation(s) PICC → CH. CT. → 137 Pit C → 12+50.

(1) ~~the~~ NRMN 14601 was not observed on the NRMN at 137 Pit C.
 (2) stored stockpile of dusty materials should be sprayed with water & covered with tarpaulin sheet. at CHA 12+50.

Reminders(s)

(1) regular cleaning of trapped dusty materials in the sedimentation tank should be conducted at pit c.
 (2) washwater should be directed to sedimentation tank for treatment before discharge (rite)

Signatures:

ET Representative	Contractor's Representative	WSD's Representative	IEC's Representative
			N/A
(Name: Christine Lai)	(Name: TUI CHING CHIU)	(Name: [unclear])	(Name: N/A)

03/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

WEEKLY ENVIRONMENTAL INSPECTION CHECKLIST

Inspection Date: 12/11/2020 Inspected by: ET: Charlene Lai WSD: Tung Kin Fai
 Contractor: Sam Ng JEC: N/A
 Inspection Time: 9:40-12:20

Weather						
Condition	<input checked="" type="checkbox"/> Sunny	<input type="checkbox"/> Fine	<input type="checkbox"/> Overcast	<input type="checkbox"/> Drizzle	<input type="checkbox"/> Rain	<input type="checkbox"/> Storm <input type="checkbox"/> Hazy
Temperature	<u>27</u> C	Humidity	<input checked="" type="checkbox"/> High	<input type="checkbox"/> Moderate	<input type="checkbox"/> Low	
Wind	<input checked="" type="checkbox"/> Calm	<input type="checkbox"/> Light	<input type="checkbox"/> Breeze	<input type="checkbox"/> Strong		

		N/A	Yes	No	Photo/Remarks
0.00	General				
0.01	Is the current Environmental Permit displayed conspicuously at all vehicle site entrances/exits for public's information at any time?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
0.02	Is ET Leader's log-book kept readily available for inspections?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.00	Construction Dust				
1.01	Are dusty materials, such as excavated materials, building debris and construction materials, and exposed earth surface properly covered to prevent dust emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.02	Are screenings, enclosures, water spraying or vacuum cleaning devices provided to dusty construction works for dust suppression?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>screening</i>
1.03	Are fumes or smoke emitting plants or construction activities shielded by a screen?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.04	Are wheel-washing facilities with high-pressure water jets provided at all site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Is wheel-washing provided to all vehicles leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are road section near the site exit free from dusty material?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.07	Are all main haul roads inside the site paved or sprayed with water to minimize dust emission during vehicle movement?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>paved</i>
1.08	Are water spraying provided immediately prior to any loading or transfer of dusty materials?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>dusty materials were kept wet to prevent dust emission</i>
1.09	Are covers provided to all dump trucks carrying dusty materials when entering and leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>No empty trucks observed</i>
1.10	Are the working areas for uprooting of trees, shrubs, or vegetation or the removal of boulders, poles, pillars sprayed with water to maintain the entire surface wet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Is exposed earth properly treated within six months after the last construction activity on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.12	Does the operation of plants on site free form dark smoke emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>N/A MG has ABTS (ABE)</i>

12/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
1.13	Are vehicles travelling at speed not exceeding 15km/hr within the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.14	Are stock of more than 20 bags of cement or day PFA covered or sheltered on top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15	Are de-bagging, batching and mixing processes of bagged cement carried out in sheltered areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are hoarding of at least 2.4m high provided along the site boundary adjoining areas accessible by the public?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Is open burning prohibited?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.00	Construction Noise (Airborne)				
2.01	Are quiet plants adopted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ QPME label
2.02	Are the PMEs operating on site well-maintained to minimize the generation of excessive noise?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ maintenance record
2.03	Are plants throttled down or turned off when not in use?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.04	Are the plants known to emit noise strongly in one direction oriented to face away from NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓ no nearby NSR
2.05	Are moveable barriers provided to screen NSRs from plant or noisy operations?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.06	Are silencers, mufflers and enclosures provided to plants?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Are the hoods, cover panels and inspection hatches of PMEs closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.08	Are purposely-built site hoarding construction with appropriate materials provided along the site boundary?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Are noisy operation properly scheduled to minimize exposure and cumulative impacts to nearby sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are valid noise emission label(s) affixed to all hand-held breakers operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Are valid noise emission label(s) affixed to all air compressors operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are all construction noise permit(s) applied for percussive piling work?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are construction noise permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are valid construction noise permit(s) displayed at all vehicular exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.00	Water Quality				
3.01	Is effluent discharge license obtained for wastewater discharge from site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.02	Is effluent discharged according to the effluent discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.03	Is wastewater discharge from site properly treated prior to discharge?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

12/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
3.04	Are perimeter channels provided to intercept storm runoff from outside the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.05	Are sand/silt removal facilities such as sand/silt traps and sediment basins provided to remove sand/silt particles from runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.06	Is surface runoff diverted to sedimentation facilities?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.07	Is the drainage system properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.08	Are construction works carefully programmed to minimize soil excavation works during rainy seasons?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.09	Are exposed soil surface protected by paving as soon as possible to reduce the potential of soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Are temporary access roads protected by crushed gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.11	Are exposed slope surface properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Is trench excavation avoided in the wet season as far as practicable, or if necessary, backfilled in short sections after excavation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.13	Are open stockpiles of construction materials on site covered by tarpaulin or similar fabric during construction?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.14	Is runoff from wheel-washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.15	Is oil leakage or spillage prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ drip tray
3.16	Are there any measures to prevent the release of oil and grease into the storm drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Obs (1)
3.17	Are the oil interceptors/grease traps properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.18	Are debris and rubbish generated on site collected, handled and disposed of properly to avoid them entering the streams?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.19	Are all fuel tanks and storage areas provided with locks and be sited on sealed areas, within bunds of capacity equal to 110% of the storage capacity of the largest tank?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.20	Are tanks, containers, storage area bunded and the locations locked as far as possible from the sensitive watercourse and stormwater drains?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.21	Are sufficient chemical toilets provided on site to handle sewage from construction work force?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.22	Are sewage disposal and toilet maintenance of the portable chemical toilets provided by the licensed contractors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.23	Is concrete washing water properly collected and treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.00	Waste Management				
4.01	Is a trip-ticket system implemented to monitor the disposal of C&D and solid wastes at public filling facilities and landfills?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

12/11

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
4.02	Is a recording system implemented to record the amount of wastes generated, recycled and disposed of?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.03	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.04	Are chemical waste separated from other waste and collected by a licensed chemical waste collector?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Are trip tickets for chemical waste disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Is chemical waste reused and recycled on site as far as practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are all containers for chemical waste properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.08	Is chemical waste storage area used solely for storage of chemical waste and properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.09	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Is the chemical waste storage area enclosed on at least 3 sides and adequately ventilated?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.11	Is an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or of 20% by volume of the chemical waste stored in that area, whichever is the greatest, provide?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Are a routine cleaning and maintenance programme implemented for drainage systems, sump pits, and oil interceptors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Are sufficient general refuse disposal/collection points provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>Dis</i>
4.15	Are appropriate measures adopted to minimize windblown litter and dust during transportation of waste?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.16	Are individual collectors for aluminum cans, plastic bottles and packaging material and office paper provided to encourage waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.17	Are C&D wastes sorted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.18	Are C&D waste disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.19	Are unused C&D materials or chemicals recycled or reused to reduce the quantity of waste?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are public fill and C&D waste reuse on site as far as practicable to avoid disposal off-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.21	Are the construction materials stored properly to minimize the potential for damage or contamination?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.22	Is a dumping license obtained to deliver public fill to public filling areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

12/11

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
5.00	Landscape and Visual				
5.01	Are Is site hoarding provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Are vegetation disturbance minimized or soil protected to reduce potential soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.03	Is construction light orientated away from the sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is grass hydroseeding provided to slopes as soon as the completion of works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Are damages to trees outside site boundary due construction works avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.06	Is excavation works carried out manually instead of machinery operation within 2.5m vicinity of any preserved trees?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.07	Are the retained and transplanted tree(s) properly protected and in good conditions?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.08	Are surgery works carried out for damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.00	Ecology				
6.01	Is site runoff properly treated to prevent any silty runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.02	Are silt trap installed and well-maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.03	Are stockpiles properly covered to avoid generating silty runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.04	Are construction works restricted to works area which are clearly defined?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7.00	Overall				
7.01	Is the EM&A properly implemented in general?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

12/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

Remark / Follow up of Observation(s) and Non-compliance(s) of Last Weekly Site Inspection:

Portion F → H.K. Velodrome L + keep sign table → 157 CH. OT → 137 P5+C → CHA + 8th




Observation(s)

13 chemicals were not placed inside a drip tray at Portion F.

Reminders (s)

(1) Housekeeping was reminded at H.K. Velodrome.

Signatures:

ET Representative	Contractor's Representative	WSD's Representative	IEC's Representative
			N/A
(Name: Charlotte Day)	(Name: Sam Ng.)	(Name: [unclear])	(Name: N/A)

12/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

WEEKLY ENVIRONMENTAL INSPECTION CHECKLIST

Inspection Date: 19/11/2020 Inspected by: ET: Charlene Lau WSD: Jaw Sai Kuen
 Inspection Time: 9:30-12:00 Contractor: Lam Tse 1412 IEC: N/A

Weather	<input checked="" type="checkbox"/> Sunny	<input type="checkbox"/> Fine	<input type="checkbox"/> Overcast	<input type="checkbox"/> Drizzle	<input type="checkbox"/> Rain	<input type="checkbox"/> Storm	<input type="checkbox"/> Hazy
Temperature	<u>28</u> °C	Humidity		<input type="checkbox"/> High	<input checked="" type="checkbox"/> Moderate	<input type="checkbox"/> Low	
Wind	<input checked="" type="checkbox"/> Calm	<input type="checkbox"/> Light	<input type="checkbox"/> Breeze	<input type="checkbox"/> Strong			

		N/A	Yes	No	Photo/Remarks
0.00 General					
0.01	Is the current Environmental Permit displayed conspicuously at all vehicle site entrances/exits for public's information at any time?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
0.02	Is ET Leader's log-book kept readily available for inspections?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.00 Construction Dust					
1.01	Are dusty materials, such as excavated materials, building debris and construction materials, and exposed earth surface properly covered to prevent dust emission?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>dusty materials were kept wet to limit dust emission</i>
1.02	Are screenings, enclosures, water spraying or vacuum cleaning devices provided to dusty construction works for dust suppression?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>enclosure</i>
1.03	Are fumes or smoke emitting plants or construction activities shielded by a screen?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.04	Are wheel-washing facilities with high-pressure water jets provided at all site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Is wheel-washing provided to all vehicles leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are road section near the site exit free from dusty material?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>Obs (2)</i>
1.07	Are all main haul roads inside the site paved or sprayed with water to minimize dust emission during vehicle movement?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.08	Are water spraying provided immediately prior to any loading or transfer of dusty materials?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>dusty materials were kept wet</i>
1.09	Are covers provided to all dump trucks carrying dusty materials when entering and leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>NO dump trucks entered</i>
1.10	Are the working areas for uprooting of trees, shrubs, or vegetation or the removal of boulders, poles, pillars sprayed with water to maintain the entire surface wet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Is exposed earth properly treated within six months after the last construction activity on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.12	Does the operation of plants on site free form dark smoke emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>N/A (No labels)</i>

19/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
1.13	Are vehicles travelling at speed not exceeding 15km/hr within the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.14	Are stock of more than 20 bags of cement or dry P/A covered or sheltered on top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15	Are de-bagging, batching and mixing processes of bagged cement carried out in sheltered areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are hoarding of at least 2.4m high provided along the site boundary adjoining areas accessible by the public?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Is open burning prohibited?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.00	Construction Noise (Airborne)				
2.01	Are quiet plants adopted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.02	Are the PMEs operating on site well-maintained to minimize the generation of excessive noise?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.03	Are plants throttled down or turned off when not in use?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.04	Are the plants known to emit noise strongly in one direction oriented to face away from NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	No construction works in this area
2.05	Are moveable barriers provided to screen NSRs from plant or noisy operations?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.06	Are silencers, mufflers and enclosures provided to plants?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	observed on 19/11
2.07	Are the hoods, cover panels and inspection hatches of PMEs closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.08	Are purpose-built site hoarding construction with appropriate materials provided along the site boundary?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Are noisy operation properly scheduled to minimize exposure and cumulative impacts to nearby sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are valid noise emission label(s) affixed to all hand-held breakers operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Are valid noise emission label(s) affixed to all air compressors operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are all construction noise permit(s) applied for percussive piling work?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are construction noise permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are valid construction noise permit(s) displayed at all vehicular exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.00	Water Quality				
3.01	Is effluent discharge license obtained for wastewater discharge from site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.02	Is effluent discharged according to the effluent discharge license?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Obs(5)
3.03	Is wastewater discharge from site properly treated prior to discharge?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Obs(5)

19/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
3.04	Are perimeter channels provided to intercept storm runoff from outside the site?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	obs (3)
3.05	Are sand/silt removal facilities such as sand/silt traps and sediment basins provided to remove sand/silt particles from runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.06	Is surface runoff diverted to sedimentation facilities?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	obs (5)
3.07	Is the drainage system properly maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	obs (4)
3.08	Are construction works carefully programmed to minimize soil excavation works during rainy seasons?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.09	Are exposed soil surface protected by paving as soon as possible to reduce the potential of soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Are temporary access roads protected by crushed gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.11	Are exposed slope surface properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Is trench excavation avoided in the wet season as far as practicable, or if necessary, backfilled in short sections after excavation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.13	Are open stockpiles of construction materials on site covered by tarpaulin or similar fabric during construction?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.14	Is runoff from wheel-washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.15	Is oil leakage or spillage prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ dripping
3.16	Are there any measures to prevent the release of oil and grease into the storm drainage system?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	obs (12)
3.17	Are the oil interceptors/ grease traps properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.18	Are debris and rubbish generated on site collected, handled and disposed of properly to avoid them entering the streams?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Reminder (1)
3.19	Are all fuel tanks and storage areas provided with locks and be sited on scaled areas, within bunds of capacity equal to 110% of the storage capacity of the largest tank?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.20	Are tanks, containers, storage area bunded and the locations locked as far as possible from the sensitive watercourse and stormwater drains?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.21	Are sufficient chemical toilets provided on site to handle sewage from construction work force?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.22	Are sewage disposal and toilet maintenance of the portable chemical toilets provided by the licensed contractors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.23	Is concrete washing water properly collected and treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.00	Waste Management				
4.01	Is a trip-ticket system implemented to monitor the disposal of C&D and solid wastes at public filling facilities and landfills?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

12/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
4.02	Is a recording system implemented to record the amount of wastes generated, recycled and disposed of?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.03	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.04	Are chemical waste separated from other waste and collected by a licensed chemical waste collector?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Are trip tickets for chemical waste disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Is chemical waste reused and recycled on site as far as practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are all containers for chemical waste properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.08	Is chemical waste storage area used solely for storage of chemical waste and properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.09	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Is the chemical waste storage area enclosed on at least 3 sides and adequately ventilated?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.11	Is an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or of 20% by volume of the chemical waste stored in that area, whichever is the greatest, provide?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Are a routine cleaning and maintenance programme implemented for drainage systems, sump pits, and oil interceptors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Are sufficient general refuse disposal/collection points provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.15	Are appropriate measures adopted to minimize windblown litter and dust during transportation of waste?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.16	Are individual collectors for aluminum cans, plastic bottles and packaging material and office paper provided to encourage waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.17	Are C&D wastes sorted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.18	Are C&D waste disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.19	Are unused C&D materials or chemicals recycled or reused to reduce the quantity of waste?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are public fill and C&D waste reuse on site as far as practicable to avoid disposal off-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.21	Are the construction materials stored properly to minimize the potential for damage or contamination?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.22	Is a dumping license obtained to deliver public fill to public filling areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

18/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
5.00	Landscape and Visual				
5.01	Are site hoarding provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Are vegetation disturbance minimized or soil protected to reduce potential soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.03	Is construction light oriented away from the sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is grass hydroseeding provided to slopes as soon as the completion of works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Are damages to trees outside site boundary due construction works avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.06	Is excavation works carried out manually instead of machinery operation within 2.5m vicinity of any preserved trees?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.07	Are the retained and transplanted tree(s) properly protected and in good conditions?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.08	Are surgery works carried out for damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.00	Ecology				
6.01	Is site runoff properly treated to prevent any silty runoff?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	obs (5)
6.02	Are silt trap installed and well-maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.03	Are stockpiles properly covered to avoid generating silty runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.04	Are construction works restricted to works area which are clearly defined?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7.00	Overall				
7.01	Is the EM&A properly implemented in general?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

19/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

Remark / Follow up of Observation(s) and Non-compliance(s) of Last Weekly Site Inspection:

Portion F → J. Pit C → 6+64 → 12+50 → ~~CHAB64~~ CHAB64




Observation(s)

- (1) ~~Chemicals~~ Chemicals were not placed in a drip tray at Portion F.
- (2) Dusty materials were observed at the site exit / Entrance at Jacking P.A.C., 6+64
- (3) Construction boundary was not ~~be~~ protected by sandbags at CHA 6+64 ~~12+50~~.
- (4) Gully was not protected by sandbags at CHA 6+64 & 12+50.
- (5) Wastewater was not treated before discharge at CHA 12+50.

Reminders(s)

- (1) Housekeeping was reminded at Portion F, pit C
- (2) Trapped materials in the gully should be cleaned regularly at Portion F.

Signatures:

ET Representative	Contractor's Representative	WSD's Representative	IEC's Representative
			N/A
(Name: Chan Man Lok)	(Name: Lam Tsz Ho)	(Name: Chan Sai Kuen)	(Name: N/A)

19/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

WEEKLY ENVIRONMENTAL INSPECTION CHECKLIST

Inspection Date: 23/11/2020

Inspected by: ET: Chau Wen Lai
 Contractor: Shing Ng

WSD: Trang Kin Fai
 IBC: Rebecca Cheung

Inspection Time: 09:30 - 12:00

Weather							
Condition	<input type="checkbox"/> Sunny	<input type="checkbox"/> Fine	<input checked="" type="checkbox"/> Overcast	<input type="checkbox"/> Drizzle	<input type="checkbox"/> Rain	<input type="checkbox"/> Storm	<input type="checkbox"/> Hazy
Temperature	<u>22.0</u> C		Humidity	<input checked="" type="checkbox"/> High	<input type="checkbox"/> Moderate	<input type="checkbox"/> Low	
Wind	<input type="checkbox"/> Calm	<input checked="" type="checkbox"/> Light	<input type="checkbox"/> Breeze	<input type="checkbox"/> Strong			

		N/A	Yes	No	Photo/Remarks
0.00	General				
0.01	Is the current Environmental Permit displayed conspicuously at all vehicle site entrances/exits for public's information at any time?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
0.02	Is ET Leader's log-book kept readily available for inspections?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.00	Construction Dust				
1.01	Are dusty materials, such as excavated materials, building debris and construction materials, and exposed earth surface properly covered to prevent dust emission?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>only wet earth work kept wet</i>
1.02	Are screenings, enclosures, water spraying or vacuum cleaning devices provided to dusty construction works for dust suppression?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>only materials work kept wet</i>
1.03	Are fumes or smoke emitting plants or construction activities shielded by a screen?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.04	Are wheel-washing facilities with high-pressure water jets provided at all site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Is wheel-washing provided to all vehicles leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are road section near the site exit free from dusty material?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.07	Are all main haul roads inside the site paved or sprayed with water to minimize dust emission during vehicle movement?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>paved</i>
1.08	Are water spraying provided immediately prior to any loading or transfer of dusty materials?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>only materials work kept wet</i>
1.09	Are covers provided to all dump trucks carrying dusty materials when entering and leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>no cover trucks observed</i>
1.10	Are the working areas for uprooting of trees, shrubs, or vegetation or the removal of boulders, poles, pillars sprayed with water to maintain the entire surface wet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Is exposed earth properly treated within six months after the last construction activity on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.12	Does the operation of plants on site free from dark smoke emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>✓ Q&MS table</i>

23/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
1.13	Are vehicles travelling at speed not exceeding 15km/hr within the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.14	Are stock of more than 20 bags of cement or day PFA covered or sheltered on top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15	Are dc-bagging, batching and mixing processes of bagged cement carried out in sheltered areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are hoarding of at least 2.4m high provided along the site boundary adjoining areas accessible by the public?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Is open burning prohibited?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.00	Construction Noise (Airborne)				
2.01	Are quiet plants adopted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ QPME label
2.02	Are the PMEs operating on site well-maintained to minimize the generation of excessive noise?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Regular inspection
2.03	Are plants throttled down or turned off when not in use?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.04	Are the plants known to emit noise strongly in one direction oriented to face away from NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	nearby NSR
2.05	Are moveable barriers provided to screen NSRs from plant or noisy operations?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.06	Are silencers, mufflers and enclosures provided to plants?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Are the hoods, cover panels and inspection hatches of PMEs closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.08	Are purposely-built site hoarding construction with appropriate materials provided along the site boundary?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Are noisy operation properly scheduled to minimize exposure and cumulative impacts to nearby sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are valid noise emission label(s) affixed to all hand-held breakers operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Are valid noise emission label(s) affixed to all air compressors operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are all construction noise permit(s) applied for percussive piling work?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are construction noise permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are valid construction noise permit(s) displayed at all vehicular exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.00	Water Quality				
3.01	Is effluent discharge license obtained for wastewater discharge from site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.02	Is effluent discharged according to the effluent discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.03	Is wastewater discharge from site properly treated prior to discharge?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

23/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
3.04	Are perimeter channels provided to intercept storm runoff from outside the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.05	Are sand/silt removal facilities such as sand/silt traps and sediment basins provided to remove sand/silt particles from runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.06	Is surface runoff diverted to sedimentation facilities?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.07	Is the drainage system properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.08	Are construction works carefully programmed to minimize soil excavation works during rainy seasons?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.09	Are exposed soil surface protected by paving as soon as possible to reduce the potential of soil erosion?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Are temporary access roads protected by crushed gravel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	panel
3.11	Are exposed slope surface properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Is trench excavation avoided in the wet season as far as practicable, or if necessary, backfilled in short sections after excavation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.13	Are open stockpiles of construction materials on site covered by tarpaulin or similar fabric during construction?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.14	Is runoff from wheel-washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.15	Is oil leakage or spillage prevented?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Obs 10
3.16	Are there any measures to prevent the release of oil and grease into the storm drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.17	Are the oil interceptors/ grease traps properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.18	Are debris and rubbish generated on site collected, handled and disposed of properly to avoid them entering the streams?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.19	Are all fuel tanks and storage areas provided with locks and be sited on sealed areas, within bunds of capacity equal to 110% of the storage capacity of the largest tank?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.20	Are tanks, containers, storage area bunded and the locations locked as far as possible from the sensitive watercourse and stormwater drains?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.21	Are sufficient chemical toilets provided on site to handle sewage from construction work force?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.22	Are sewage disposal and toilet maintenance of the portable chemical toilets provided by the licensed contractors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.23	Is concrete washing water properly collected and treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.00	Waste Management				
4.01	Is a trip-ticket system implemented to monitor the disposal of C&D and solid wastes at public filling facilities and landfills?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
4.02	Is a recording system implemented to record the amount of wastes generated, recycled and disposed of?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.03	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.04	Are chemical waste separated from other waste and collected by a licensed chemical waste collector?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Are trip tickets for chemical waste disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Is chemical waste reused and recycled on site as far as practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are all containers for chemical waste properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.08	Is chemical waste storage area used solely for storage of chemical waste and properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.09	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Is the chemical waste storage area enclosed on at least 3 sides and adequately ventilated?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.11	Is an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or of 20% by volume of the chemical waste stored in that area, whichever is the greatest, provide?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Are a routine cleaning and maintenance programme implemented for drainage systems, sump pits, and oil interceptors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Are sufficient general refuse disposal/collection points provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.15	Are appropriate measures adopted to minimize windblown litter and dust during transportation of waste?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.16	Are individual collectors for aluminum cans, plastic bottles and packaging material and office paper provided to encourage waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.17	Are C&D wastes sorted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.18	Are C&D waste disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.19	Are unused C&D materials or chemicals recycled or reused to reduce the quantity of waste?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are public fill and C&D waste reuse on site as far as practicable to avoid disposal off-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.21	Are the construction materials stored properly to minimize the potential for damage or contamination?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.22	Is a dumping license obtained to deliver public fill to public filling areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

23/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

		N/A	Yes	No	Photo/Remarks
5.00	Landscape and Visual				
5.01	Are Is site hoarding provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Arc vegetation disturbance minimized or soil protected to reduce potential soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.03	Is construction light oriented away from the sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is grass hydroseeding provided to slopes as soon as the completion of works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Are damages to trees outside site boundary due construction works avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.06	Is excavation works carried out manually instead of machinery operation within 2.5m vicinity of any preserved trees?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.07	Are the retained and transplanted tree(s) properly protected and in good conditions?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<i>removal</i>
5.08	Are surgery works carried out for damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.00	Ecology				
6.01	Is site runoff properly treated to prevent any silty runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.02	Are silt trap installed and well-maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.03	Are stockpiles properly covered to avoid generating silty runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.04	Are construction works restricted to works area which are clearly defined?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7.00	Overall				
7.01	Is the EM&A properly implemented in general?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

23/11



Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.
O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O

Remark / Follow up of Observation(s) and Non-compliance(s) of Last Weekly Site Inspection:

Hk. vegetation (pit L-M-N-O)





Observation(s)

(1) oil spillage was found at pit L at Hong Kong vegetation.

Reminder(s)

(1) All trees that are decided as "retain" should have sufficient protection.
x / Fences erected should enclose the retain tree, including the posts.
while surround of the protection barrier

Signatures:

ET Representative	Contractor's Representative	WSD's Representative	IEC's Representative
			
(Name: <i>Charmene</i>)	(Name: <i>Sandy</i>)	(Name: <i>Alan</i>)	(Name: <i>Heonnie</i>)

23/11

Appendix M

Proactive Environmental Protection Proforma

Proactive Environmental Protection for the Next Reporting Month

Reporting Period	Activity	Major Environmental Impact	Environmental Mitigation Measure
1 December 2020 - 31 December 2020	<ul style="list-style-type: none"> - Excavation of trench - Mainlaying of pipe - Backfilling of the trench - Work fronts for open trench - Work fronts for pipe jacking - Pile sheet driving works - Grouting works 	Construction dust and noise generation; construction wastes	<ul style="list-style-type: none"> - Dust suppression by regular wetting and water spraying - Reduction of noise from equipment and machinery on-site - Sorting and storage of general refuse and construction waste

Appendix N

Impact Monitoring Schedule of Next Reporting Month (Tentative)

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



Dec-20						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
		1	2	3 Impact Monitoring	4	5
6	7	8	9 Impact Monitoring	10	11	12
13	14	15 Impact Monitoring	16	17	18	19
20	21 Impact Monitoring	22	23	24	25	26
27	28	29	30	31 Impact Monitoring		

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Appendix O

Academic Calendar(s)

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
Monthly EM&A Report No.28



CREATIVE SECONDARY SCHOOL CALENDAR 2020-2021

	Su	Mo	Tu	We	Th	Fr	Sa	
August		9	10	11	12	13	14	15
		16	17	18	19	20	21	22
1	23	24A	25B	26C	27D	28E	29	19/8 First School day
	30	31F						
September	2		1	2A	3B	4C		1/9 Staff Development Day 1
3	6	7	8D	9E	10F	11A	12	Legco election 6 Sep, EDB declare 7/9 as school holiday
	13	14B	15C	16D	17E	18F	19	18/09 Swimming gala
4	20	21A	22B	23C	24D	25E	26	
5	27	28F	29A	30B				
October								3 1/10 National Day, 2/10 The Day following Mid-Autumn Festival
4	5C	6D	7E	8F	9A			
6	11	12B	13C	14D	15E	16F	17	
	18	19	20	21	22	23	24	19-24 Term Break
7	25	26	27A	28B	29C	30D	31	26/10 Chung Yung Festival Holiday.
November	8	1	2E	3F	4A	5B	6C	7 5/ 11 University Fair
	8	9	10D	11E	12F	13A	14	9/11/2020 Staff Development Day 2
	9	15	16B	17C	18D	19E	20F	21
10	22	23A	24B	25C	26D	27E	28	
	29	30F						
December	11		1A	2B	3C	4	5	04/12 Sports Day
12	6	7D	8E	9F	10A	11B	12	
	13	14C	15D	16E	17F	18A	19	
	20	21	22	23	24			25/12 Christmas Day 16/12 The First Weekday after Christmas Day
	27	28	29	30	31			21/12-2/1 Christmas & New Year Holiday
January							2	1/1 New Year's Day
13	3	4B	5C	6D	7E	8F	9	
14	10	11A	12B	13C	14D	15E	16	
15	17	18F	19A	20B	21C	22D	23	
16	24	25E	26F	27A	28B	29C	30	
	31							
February	17		1D	2E	3F	4A	5B	6
	7	8C	9D	10	11	12	13	12-15 New year Holiday. 10-20/2 Chinese New Year Holiday
	14	15	16	17	18	19	20	
18	21	22E	23F	24A	25B	26C	27	
	28							
March	19		1D	2E	3F	4A	5B	6
	7	8C	9D	10E	11F	12A	13	
20	14	15B	16C	17D	18E	19F	20	
	21	22	23	24	25	26	27	Creative Week
21	28	29A	30B	31C				
April								01/04-10/04 Easter Holiday, 02/04 Good Friday, 03/04 The Day following Good Friday
	4	5	6	7	8	9	10	04/04 Ching Ming Festival, 05/04 Easter Monday
22	11	12D	13E	14F	15A	16B	17	
	18	19C	20D	21E	22F	23A	24	
23	25	26B	27C	28D	29E	30F		
May								Labour Day
24	2	3A	4B	5C	6D	7E	8	
25	9	10F	11A	12B	13C	14D	15	
26	16	17E	18F	19A	20B	21C	22	Birthday of Buddha
	23	24C	25D	26E	27F	28A	29	
27	30	31B						
June				1C	2D	3E	4F	5
28	6	7A	8B	9C	10D	11E	12	
29	13	14	15F	16A	17B	18C	19	14/06 Tuen Ng Festival
30	20	21D	22E	23F	24A	25B	26	
	27	28C	29D	30E				
July								01/07 HKSAR Establishment Day
	4	5	6	7	8	9	10	
	11	12	13	14	15	16	17	
	18	19	20	21	22	23	24	
	25	26	27	28	29	30	31	
August								
	1	2	3	4	5	6	7	
	8	9	10	11	12	13	14	
	15	16	17	18	19	20	21	
	22	23	24	25	26	27	28	
	29	30	31					

Total number of school days: 189days	Total number of school holidays: 93days
Total number of additional discretionary holidays: 0 day	Total number of Staff development days (no school) : 3 days

Remark: 1st Trimester: 24 Aug 2020 - 20 Nov 2020; 2nd Trimester: 23 Nov 2020 - 3 Mar 2021; 3rd Trimester: 4 Mar 2021 - 4 Jun 2021
 (For Form 1/ Form 2 Arts and Technology and Form 3 Science)

School Day
Public Holiday
School Holiday
Staff Development Day
Sunday
Saturday

Appendix P

Interim Report for the Complaint

Interim Report on Environmental Complaint

Project Title	Proposed Desalination Plant in TKO Area 137 for Contract 13/WSD/16 Mainlaying in Tseung Kwan O
Source of Complaint	Letter from EPD (Ref. No. N08/RE/00026710-20) dated 23 Nov 2020.
Location of Incident	Construction Site at Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T.
Complaint Code	13/WSD/16_C001
Complaint description	<p>EPD has received the complaint of suspected construction noise from the construction site at Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T.</p> <p>It was also suspected that powered mechanical equipment such as roller and dump truck was used at the site for the purpose of carrying out construction works on 15 November 2020 (Sunday).</p>
Investigation finding	<p>Our Environmental Team under WSD Contract No. 13/WSD/16 carried out the complaint investigation from 23 November 2020. The contractor has been requested to provide us with the relevant site inspection records/dairy, site photos, valid Construction Noise Permit (CNP) and PME details for complaint investigation from 23 Nov. 2020, apart from the CNP (see the valid CNP in Appendix B), we have not received the site inspection records/diary and site photos up to the date of joint meeting which has invited Independent Environmental Checker, WSD and the Contractors (see the attached email records).</p> <p>On 2 December 2020, we held the joint site audit and meeting with WSD representatives and the Environmental Officer, Mr. Calvin Chik of Penta Ocean (hereafter referred to the Contractor) for following up the complaint investigation, the Contractor has admitted that the suspected construction works were being carried out from 9am to 2pm on 15 November 2020 and confirmed that no method statement was submitted to WSD for the woks carried out on 15 November 2020.</p> <p>The contractor informed that the concerned construction work was only remedial works for deteriorated grasscrete road inside the TKO Landfill Stage 1 near TKO South Waterfront Promenade on the day of complaint arising but the works were undertaken in accordance with the approved time allowed for work during restricted hours as specified in the CNP. The Contractor claimed that no information including site photos and PME details could be provided to us, ET requested they should give the relevant information for our investigation.</p> <p>As confirmed by WSD, the works carried out on 15 November 2020 was an additional work under the same Work Contract 13/WSD/16 and the concerned work was not related to “a dedicated trunk feed system water minas for the transfer of fresh water output from the desalination plant to the existing Tsuen Kwan O Fresh Water Primary Service Reservoir in Po Lam”. (see the attached email records in Appendix A).</p> <p>So far, we concluded the responsible Contractor applied the CNP to</p>

	carry out the construction work within restricted hours but there should be more evidence to be provided by the Contractor to demonstrate their compliance with the CNP.
Actions taken / to be taken	The responsible contractor has been recommended, if any additional works to be carried in the future, should notify ET, Engineering Representative (i.e. WSD) and IEC of relevant method statements prior to commencement of the additional works for evaluation of sufficient and effective environmental mitigation measures and pollution controls to be taken for the additional works. ET will perform site audits for any additional works if considered necessary.
Prepared by	Karen Cheung
Certified by	Jacky Leung
Date	2 December 2020

Appendix A: Supporting email records

Karen Cheung

From: Karen Cheung <kcheung@acuityhk.com>
Sent: Wednesday, 2 December 2020 7:14 pm
To: 'yui_him_wong@wsd.gov.hk'
Cc: 'Adi LEE | ANewR'; 'ASCL Charlene Lai'; 'Gideon Cheng'; 'James Chim'; 'Jacky C H Leung'; 'James Choi'; 'Jacky CHOW'; 'Calvin Chik'; 'Melvin Tsang'; 'kli@acuityhk.com'; 'Kwok Kee Yuen'; 'ntsui@acuityhk.com'; 'Project ASCL'; 'Rex Man'; 'Reasonlie CHEUNG | ANewR'; 'Sam Ng'; 'Thomas Tiu'; 'Vega Wong'; 'kf_cheng@wsd.gov.hk'; 'paul_cy_lee@wsd.gov.hk'; 'janice_wai_yan_lai@wsd.gov.hk'; 'issac_ho_wai_hui@wsd.gov.hk'
Subject: RE: Complaint of Construction Noise during Restricted Hours from the Construction Site at Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T. (WSD Contract No. 13/WSD/16)///

Dear Tim ,

Thank you for your email,

Referring to your email as below and the meeting this morning, the concerned work is an additional work under the same Work Contract 13/WSD/16.

Please be reminded that the responsible contractor(s) or subcontractor(s) of any additional works under the same contract (CN 13/WSD/16) should submit, before work commencement, the relevant method statement including environmental mitigation measures to ET for review and certification and then IEC for verification so as to comply with the statutory requirements of the EP, the EIA report and the EM&A Manual. It is friendly reminded to comply with the CNP requirements strictly when carrying out any reported works during restricted hours.

According to the requirement of the EM&A Manual, the responsible contractor i.e. Penta Ocean has been reminded to provide us the relevant site inspection records and site photos for complaint investigation from 23 Nov. 2020 but we have not received the information up to now. Gratefully please help us to seek the relevant site records from Penta Ocean before COB tomorrow i.e. 3 December 2020.

Should you have any question, please feel free to contact me through 2698-9097.

Best regards,

Karen Cheung

Acuity Sustainability Consulting Limited
Unit C, 11/F, Ford Glory Plaza, No. 37-39 Wing Hong Street,
Cheung Sha Wan, Kowloon, H.K.
Website: www.acuityhk.com
O: 2698-9097 | F: 2333-1316

Please consider the Environment before printing this Email

From: yui_him_wong@wsd.gov.hk <yui_him_wong@wsd.gov.hk>
Sent: Wednesday, 2 December 2020 2:06 pm
To: Karen Cheung <kcheung@acuityhk.com>
Cc: 'Adi LEE | ANewR' <aymlee@anewr.com>; 'ASCL Charlene Lai' <clai@acuityhk.com>; 'Gideon Cheng' <gideon.cheng@mail.penta-ocean.co.jp>; 'James Chim' <jameschim@ccl-concentric.com>; 'Jacky C H Leung'

<jleung@acuityhk.com>; 'James Choi' <jpschoi@anewr.com>; 'Jacky CHOW' <jtkchow@anewr.com>; 'Calvin Chik' <kacheong.chik@mail.penta-ocean.co.jp>; 'Melvin Tsang' <kin_fai_tsang@wsd.gov.hk>; kli@acuityhk.com; 'Kwok Kee Yuen' <kwokkee.yuen@mail.penta-ocean.co.jp>; ntsui@acuityhk.com; 'Project ASCL' <project@acuityhk.com>; 'Rex Man' <rex.man@mail.penta-ocean.co.jp>; 'Reasonlie CHEUNG | ANewR' <ryycheung@anewr.com>; 'Sam Ng' <sam.ng@mail.penta-ocean.co.jp>; 'Thomas Tiu' <thomas.tiu@mail.penta-ocean.co.jp>; 'Vega Wong' <vwong@acuityhk.com>; yui_him_wong@wsd.gov.hk; kf_cheng@wsd.gov.hk; paul_cy_lee@wsd.gov.hk; janice_wai_yan_lai@wsd.gov.hk; issac_ho_wai_hui@wsd.gov.hk
Subject: RE: Complaint of Construction Noise during Restricted Hours from the Construction Site at Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T. (WSD Contract No. 13/WSD/16)///

Dear Karen,

Further to our meeting in this morning, please be confirmed that the concerned works carried on 15 Nov 2020 was not related to "a dedicated trunk feed system including about 9km long water mains for the transfer of fresh water output from the desalination plant to the existing Tseung Kwan O Fresh Water Primary Service Reservoir in Po Lam" under CN13/WSD/16.

Best Regards

WONG Yui-him, Tim
E/C(5)
Construction Division
Water Supplies Department

Tel: 2152 5742(Office), 3650 3418(Site), 5122 8825(Mobile)

From: "Karen Cheung" <kcheung@acuityhk.com>
To: "'Calvin Chik'" <kacheong.chik@mail.penta-ocean.co.jp>, "'Tim Wong'" <yui_him_wong@wsd.gov.hk>, "'Reasonlie CHEUNG | ANewR'" <ryycheung@anewr.com>
Cc: "'Hivan Cheng'" <kf_cheng@wsd.gov.hk>, "'Melvin Tsang'" <kin_fai_tsang@wsd.gov.hk>, "'Vega Wong'" <vwong@acuityhk.com>, "'Project ASCL'" <project@acuityhk.com>, "'Sam Ng'" <sam.ng@mail.penta-ocean.co.jp>, "'Rex Man'" <rex.man@mail.penta-ocean.co.jp>, "'Jacky C H Leung'" <jleung@acuityhk.com>, "'ASCL Charlene Lai'" <clai@acuityhk.com>, <kli@acuityhk.com>, <ntsui@acuityhk.com>, "'Thomas Tiu'" <thomas.tiu@mail.penta-ocean.co.jp>, "'Kwok Kee Yuen'" <kwokkee.yuen@mail.penta-ocean.co.jp>, "'Tim Wong'" <yui_him_wong@wsd.gov.hk>, "'Gideon Cheng'" <gideon.cheng@mail.penta-ocean.co.jp>, "'James Chim'" <jameschim@ccl-concentric.com>, "'Reasonlie CHEUNG | ANewR'" <ryycheung@anewr.com>, "'Jacky CHOW'" <jtkchow@anewr.com>, "'Adi LEE | ANewR'" <aymlee@anewr.com>, "'James Choi'" <jpschoi@anewr.com>
Date: 01/12/2020 19:04
Subject: RE: Complaint of Construction Noise during Restricted Hours from the Construction Site at Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T. (WSD Contract No. 13/WSD/16)///

Dear All,

In reference to the information provided by the Contractor on 1 December 2020, the construction works carried out on 15 November 2020 was "requested by WSD to carry out remedial works for the deteriorated grasscrete road inside the TKO Landfill Stage 1 near TKO South Waterfront Promenade. The work locations for the remedial works are within the area under maintenance by EPD and it is not the construction site for the works under 13/WSD/16." Could WSD confirm whether the works carried out on 15 November 2020 are

related to 13/WSD/16 -“a dedicated trunk feed system including about 9km long water mains for the transfer of fresh water output from the desalination plant to the existing Tseung Kwan O Fresh Water Primary Service Reservoir in Po Lam.”? In addition, Contractor please provide a site plan with highlighting the works area carried out on 15 November 2020 to confirm the location of the site works.

In order to facilitate the investigation progress, a joint site walk and a meeting are proposed among IEC, WSD, ET and Contractor. The site walk will be meet up in the site office at 9am, and the meeting will be held in the site office after the site walk, around 10:30am, please IEC, WSD and contractor confirm your availability through this email. Can Contractor (Calvin) please arrange the walk including the work area that carried out on 15 November 2020 for our investigation? Thank You.

Please be reminded according to the EM&A Manual Section 13.3 “During the complaint investigation work, the Contractor and ER shall cooperate with the ET Leader in providing all necessary information and assistance for completion of the investigation. If mitigation measures are identified in the investigation, the Contractor should promptly carry out the mitigation measures. EPD will approve the proposed mitigation measures and the ET Leader and IEC should check that the measures have been carried out by the Contractor.”

Should you have any question, please feel free to contact me through 2698-9097.

Best regards,

Karen Cheung

Acuity Sustainability Consulting Limited
Unit C, 11/F, Ford Glory Plaza, No. 37-39 Wing Hong Street,
Cheung Sha Wan, Kowloon, H.K.
Website: www.acuityhk.com
O: 2698-9097 | F: 2333-1316

Please consider the Environment before printing this Email

From: Calvin Chik <kacheong.chik@mail.penta-ocean.co.jp>
Sent: Tuesday, 1 December 2020 6:00 pm
To: Karen Cheung <kcheung@acuityhk.com>
Cc: Hivan Cheng <kf_cheng@wsd.gov.hk>; Melvin Tsang <kin_fai_tsang@wsd.gov.hk>; Vega Wong <vwong@acuityhk.com>; Project ASCL <project@acuityhk.com>; Sam Ng <sam.ng@mail.penta-ocean.co.jp>; Rex Man <rex.man@mail.penta-ocean.co.jp>; Jacky C H Leung <jleung@acuityhk.com>; ASCL Charlene Lai <clai@acuityhk.com>; kli@acuityhk.com; ntsui@acuityhk.com; Thomas Tiu <thomas.tiu@mail.penta-ocean.co.jp>; Kwok Kee Yuen <kwokkee.yuen@mail.penta-ocean.co.jp>; Tim Wong <yui_him_wong@wsd.gov.hk>; Gideon Cheng <gideon.cheng@mail.penta-ocean.co.jp>; James Chim <jameschim@ccl-concentric.com>; Reasonlie CHEUNG | ANewR <ryycheung@anewr.com>; Jacky CHOW <jtkchow@anewr.com>; Adi LEE | ANewR <aymlee@anewr.com>; James Choi <jpschoi@anewr.com>
Subject: Re: Complaint of Construction Noise during Restricted Hours from the Construction Site at Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T. (WSD Contract No. 13/WSD/16)///

Dear Karen,

Below some information regarding the captioned complaint case for your reference.

We were instructed by WSD under letter reference dated 31 Aug 2020 (refer to attached letter with location layout) to carry out remedial works for the deteriorated grasscrete road inside the TKO Landfill Stage 1 near TKO South Waterfront Promenade. The locations for the remedial works are within the area under maintenance by EPD and it is not the construction site for the works under 13/WSD/16.

The nature of the remedial work is to cover up the deteriorated road surface by cold asphalt on top and to be compacted further. Since it is not possible to maintain the traffic of the road during the remedial works, temporary road blockage is required, as such we are only allowed to carry out the works by either Sunday or public holidays due to the traffic issue. We applied CNP for the works and the conditions stated in the CNP were already conveyed to the subcontractor to strictly follow including the allowable working period and the usage of designated plants/machines.

Unfortunately, a complaint from the public was received as the public may not be aware that we have already applied a valid CNP to conduct the works.

Regards,
Calvin Chik
Penta-Ocean - Concentric Joint Venture
Contract No: 13/WSD/16
Mobile: 9863 5630

Karen Cheung

From: Calvin Chik <kacheong.chik@mail.penta-ocean.co.jp>
Sent: Monday, 30 November 2020 12:08 pm
To: Karen Cheung
Cc: Hivan Cheng; Melvin Tsang; Vega Wong; Project ASCL; Sam Ng; Rex Man; Jacky C H Leung; ASCL
Charlene Lai; kli@acuityhk.com; ntsui@acuityhk.com; Thomas Tiu; Kwok Kee Yuen; Tim Wong;
Gideon Cheng; James Chim
Subject: Re: Complaint of Construction Noise during Restricted Hours from the Construction Site at Tseung
Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T. (WSD
Contract No. 13/WSD/16)///
Attachments: I-1249 EPD.pdf; photo.jpeg

Dear Karen,

Please find the attached CNP for the works.

Further to the complaint case, we have implemented noise enclosure as mitigation measures to reduce nuisance to the public at the concerned locations as shown in the attached record photo for your reference.

Since we are now being invited by EPD to attend the interview for explanation/clarification regarding the complaint, we are sorry to inform you that we cannot provide you any further information at this moment as this case may enter legal procedure.

Regards,

Calvin Chik

Penta-Ocean - Concentric Joint Venture

Contract No: 13/WSD/16

Mobile: 9863 5630

Karen Cheung <kcheung@acuityhk.com> 於 2020 年 11 月 27 日 週五 下午 6:24 寫道 :

Dear Calvin,

As per our conversation this afternoon, please provide the supporting documents to avoid any delay for response to EPD, thank you.

Should you have any question, please feel free to contact me through 2698-9097.

Best regards,

Karen Cheung

Acuity Sustainability Consulting Limited

Unit C, 11/F, Ford Glory Plaza, No. 37-39 Wing Hong Street,

Cheung Sha Wan, Kowloon, H.K.

Website: www.acuityhk.com

O: 2698-9097 | F: 2333-1316

Please consider the Environment before printing this Email

From: Karen Cheung <kcheung@acuityhk.com>

Sent: Monday, 23 November 2020 4:47 pm

To: 'kf_cheng@wsd.gov.hk' <kf_cheng@wsd.gov.hk>; 'Calvin Chik' <kacheong.chik@mail.penta-ocean.co.jp>; 'Adi Lee' <aymlee@anewr.com>

Cc: 'kin_fai_tsang@wsd.gov.hk' <kin_fai_tsang@wsd.gov.hk>; 'Vega Wong' <vwong@acuityhk.com>; 'Project ASCL' <project@acuityhk.com>; 'James Choi' <jpschoi@anewr.com>; 'sam.ng@mail.penta-ocean.co.jp' <sam.ng@mail.penta-ocean.co.jp>; '[yanting.chong@mail.penta-ocean.co.jp](mailto:yantin.chong@mail.penta-ocean.co.jp)' <[yanting.chong@mail.penta-ocean.co.jp](mailto:yantin.chong@mail.penta-ocean.co.jp)>; 'rex.man@mail.penta-ocean.co.jp' <rex.man@mail.penta-ocean.co.jp>; 'kenng@ccl-concentric.com' <kenng@ccl-concentric.com>; 'Jacky C H Leung' <jleung@acuityhk.com>; 'Nelson Tsui' <ntsui@acumen-env.com>; 'ASCL Charlene Lai' <clai@acuityhk.com>

Subject: FW: Complaint of Construction Noise during Restricted Hours from the Construction Site at Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T. (WSD Contract No. 13/WSD/16)

Dear Calvin,

A compliant has been received by EPD and concerning with the noise emission on 15 November at the TKO stage 1 near Jockey club HKFA football training center. Referring to the email from EPD on 23 November, please provide the below information for our investigation by tomorrow, thank you:

1. CNP

2. site diary on 15 November 2020

4. photos during construction works on 15 November 2020

Should you have any question, please feel free to contact me through 2698-9097.

Best regards,

Karen Cheung

Acuity Sustainability Consulting Limited

Unit C, 11/F, Ford Glory Plaza, No. 37-39 Wing Hong Street,

Cheung Sha Wan, Kowloon, H.K.

Website: www.acuityhk.com

O: 2698-9097 | F: 2333-1316

Please consider the Environment before printing this Email

From: kiuchungtse@epd.gov.hk <kiuchungtse@epd.gov.hk>

Sent: Monday, 23 November 2020 1:44 pm

To: kf_cheng@wsd.gov.hk

Cc: kcheung@acuityhk.com; jleung@acuityhk.com; ryycheung@anewr.com; jpschoi@anewr.com; smchiu@epd.gov.hk; ylko@epd.gov.hk

Subject: Complaint of Construction Noise during Restricted Hours from the Construction Site at Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T. (WSD Contract No. 13/WSD/16)

Dear Mr. CHENG / WSD,

We received a complaint from a member of the public with concern on construction noise associated with the captioned construction site. It was suspected that powered mechanical equipment such as roller and dump truck was used for the purpose of carrying out construction works on 15 November 2020 (Sunday). We have issued a letter inviting the contractor to attend an interview with us and copied to WSD which is attached for your advance information.

If the Engineer and the Engineer's Representative has any information to provide regarding the

above incident, please feel free to contact our Ms. Suman CHIU at 2117 7535 or the undersigned.

By copy of this email, the complaint is now referred to the ET Leader for action. Please follow the complaint handling procedure in accordance with the EM&A Manual, and submit an interim report to us on the status of the complaint investigation and follow-up action on or before 4.12.2020. Thanks.

Best Regards,
KC Tse
E(RE)42, EPD
Tel: 2117 7530
23.11.2020

Appendix B: Construction Noise Permit for the works carried out on 15 November 2020

FORM 3
NOISE CONTROL ORDINANCE
(Chapter 400)
SECTION 8(9)

[reg.5(a)]

**CONSTRUCTION NOISE PERMIT FOR THE USE OF POWERED
MECHANICAL EQUIPMENT FOR THE PURPOSE OF CARRYING OUT
CONSTRUCTION WORK OTHER THAN PERCUSSIVE PILING AND/OR
THE CARRYING OUT OF PRESCRIBED CONSTRUCTION WORK**

CONSTRUCTION NOISE PERMIT NO. GW-RE0927-20

To : PENTA-OCEAN – CONCENTRIC JOINT VENTURE (PENTA-OCEAN CONSTRUCTION CO., LTD. and CONCENTRIC
CONSTRUCTION LIMITED as partners)

This construction noise permit is issued in accordance with section 8 of the Noise Control Ordinance. Permission is granted for the use of powered mechanical equipment for the purpose of carrying out construction work other than percussive piling and/or the carrying out of prescribed construction work, subject to the conditions set out below. The carrying out of construction work otherwise than in accordance with the conditions may result in the permit being cancelled and in a prosecution for an offence.

CONDITIONS

1. Construction site where the powered mechanical equipment and/or prescribed construction work may be employed:

Full address: Tseung Kwan O Stage 1 Landfill near Jockey Club HKFA Football Training Centre, Tseung Kwan O, N.T.
(WSD Contract No. 13/WSD/16). Lot No.: ---

The site boundary, that is, the boundary of the area within which the powered mechanical equipment may be used and the prescribed construction work may be carried out is delineated on the attached plan which forms part of this construction noise permit.

2. ~~PART~~/WHOLE of the site falls * ~~WITHIN~~/OUTSIDE a designated area.
3. Powered Mechanical Equipment

- a. Items of powered mechanical equipment which may be used inside the site boundary :

<i>Identification code of item of powered mechanical equipment (if applicable)</i>	<i>Description of item of powered mechanical equipment</i>	<i>No. of units</i>
CNP 050	Compactor, vibratory	One
CNP 169	Power rammer (petrol)	One

- b. Validity of the construction noise permit for the use of the powered mechanical equipment:

Date and time of commencement : 1 November 2020 at 0700 hours

Days and hours : 0000-2400 hours on general holiday (including Sunday), 0000-0700 hours and 1900-2400 hours on any day not being a general holiday [but note Condition 3.d.1 below for the operating hours within which the use of the above listed powered mechanical equipment is allowed].

This part of the permit expires on : 24 January 2021 at 1900 hours

- c. One photograph, endorsed by the Authority, of each item of powered mechanical equipment described in this construction noise permit is required to be kept on the construction site and made available for inspection by the Authority.
d. Other conditions imposed on the use of the powered mechanical equipment :

1. The powered mechanical equipment listed in condition 3.a. shall only be operated during the hours shown below:

<u>General holiday (including Sunday)</u>	<u>0700 – 1900 hours</u>
---	--------------------------

4. Prescribed Construction Work

a. Type of prescribed construction work which may be carried out inside the site boundary :

<i>Identification code of type of prescribed construction work</i>	<i>Description of type of prescribed construction work</i>
	Not applicable

b. Validity of the construction noise permit for the carrying out of the prescribed construction work:

Date and time of commencement: Not applicable at Not applicable

Days and hours: Not applicable

This part of the permit expires on : Not applicable at Not applicable

c. ~~Site layout plan(s), endorsed by the Authority, may be attached with the permit to indicate the locations permitted for the carrying out of prescribed construction work described in this permit. The layout plan(s) is(are) required to be kept on the construction site and made available for inspection by the Authority.~~

d. Other conditions imposed on the carrying out of the prescribed construction work:

5. This construction noise permit or a copy thereof must be displayed on the construction site at conspicuous location for public information.

Dated this 30th day of October 20 20



Signed : _____
(WONG Mei-chi)
for Authority

* Delete as necessary

表格 3
噪音管制條例
(第 400 章)
第 8(9) 條

[第 5(a) 條]

建築噪音許可證
為進行建築工程 (撞擊式打樁除外)
而使用機動設備及 / 或進行訂明建築工程

建築噪音許可證編號: GW-RE0927-20

致: 五洋協力聯營 (PENTA-OCEAN CONSTRUCTION CO., LTD. 及 協力建業有限公司為合伙人)

本建築噪音許可證是按照《噪音管制條例》第 8 條的規定而發出的。現准予使用機動設備以進行撞擊式打樁工程以外的建築工程及 / 或進行訂明建築工程, 但須受以下條件規限。若不按照該等條件進行建築工程, 許可證可遭撤銷, 而且會受到檢控。

條 件

1. 可使用機動設備及 / 或進行訂明建築工程的建築地盤:

詳細地址: 新界將軍澳將軍澳第一期堆填區近賽馬會香港足球總會足球訓練中心(水務署合約編號 13/WSD/16)。地段編號: ---

地盤範圍(即可使用機動設備及進行訂明建築工程的地方範圍)已描劃於夾附的圖則上, 而該圖則是本建築噪音許可證的一部分。

2. 該地盤部分 / 全部*位於指定範圍之內 / 外*。
3. 機動設備

- a. 在地盤範圍內可使用的各項機動設備:

各項機動設備的識別代碼 (如適用的話)	各項機動設備的說明	數目
CNP 050	壓實機, 震動式	壹
CNP 169	機動夯土機(汽油)	壹

- b. 可使用機動設備的建築噪音許可證有效期:

生效日期及時間: 二零二零年十一月一日上午七時

日期及時間: 公眾假日(包括星期日)的凌晨零時至晚上十二時, 公眾假日以外的任何一日凌晨零時至上午七時及下午七時至晚上十二時【但須注意條件3.d.1.有關可以使用上列機動設備的時間】。

此部分許可證屆滿日期及時間: 二零二一年一月二十四日下午七時
日期 時間

- c. 建築地盤須備有本建築噪音許可證所述每件機動設備的照片各一幀, 供監督隨時查看; 該等照片須經監督認可。
d. 規限使用機動設備的其他條件:
1. 祇可於以下時間內使用列在條件3.a.內的機動設備:

公眾假日(包括星期日)	上午七時至下午七時
-------------	-----------

4. 訂明建築工程

a. 在地盤範圍內可進行的訂明建築工程：

訂明建築工程的識別代碼	訂明建築工程的類別的說明
	不適用

b. 可進行訂明建築工程的建築噪音許可證有效期：

生效日期及時間：不適用

日期及時間：不適用

此部分許可證屆滿日期及時間：不適用
日期 時間

c. 本許可證可夾附經監督認可的地盤圖則，以顯示本許可證准予進行訂明建築工程的地點。該地盤圖則須存放於建築地盤供監督隨時查看。

d. 規限進行訂明建築工程的其他條件：

5. 本建築噪音許可證或其副本必須展示於建築地盤的當眼位置，給予公眾人士參閱。

日期：20 20 年 10 月 30 日



簽署：_____

監督
(王美枝代行)

* 刪去不適用者

Photograph(s) attached to Construction Noise Permit No. GW-RE0927-20
建築噪音許可證編號：GW-RE0927-20 的照片




CNP 050 Compactor, vibratory
壓實機，震動式



CNP 169 Power rammer (petrol)
機動夯土機 (汽油)



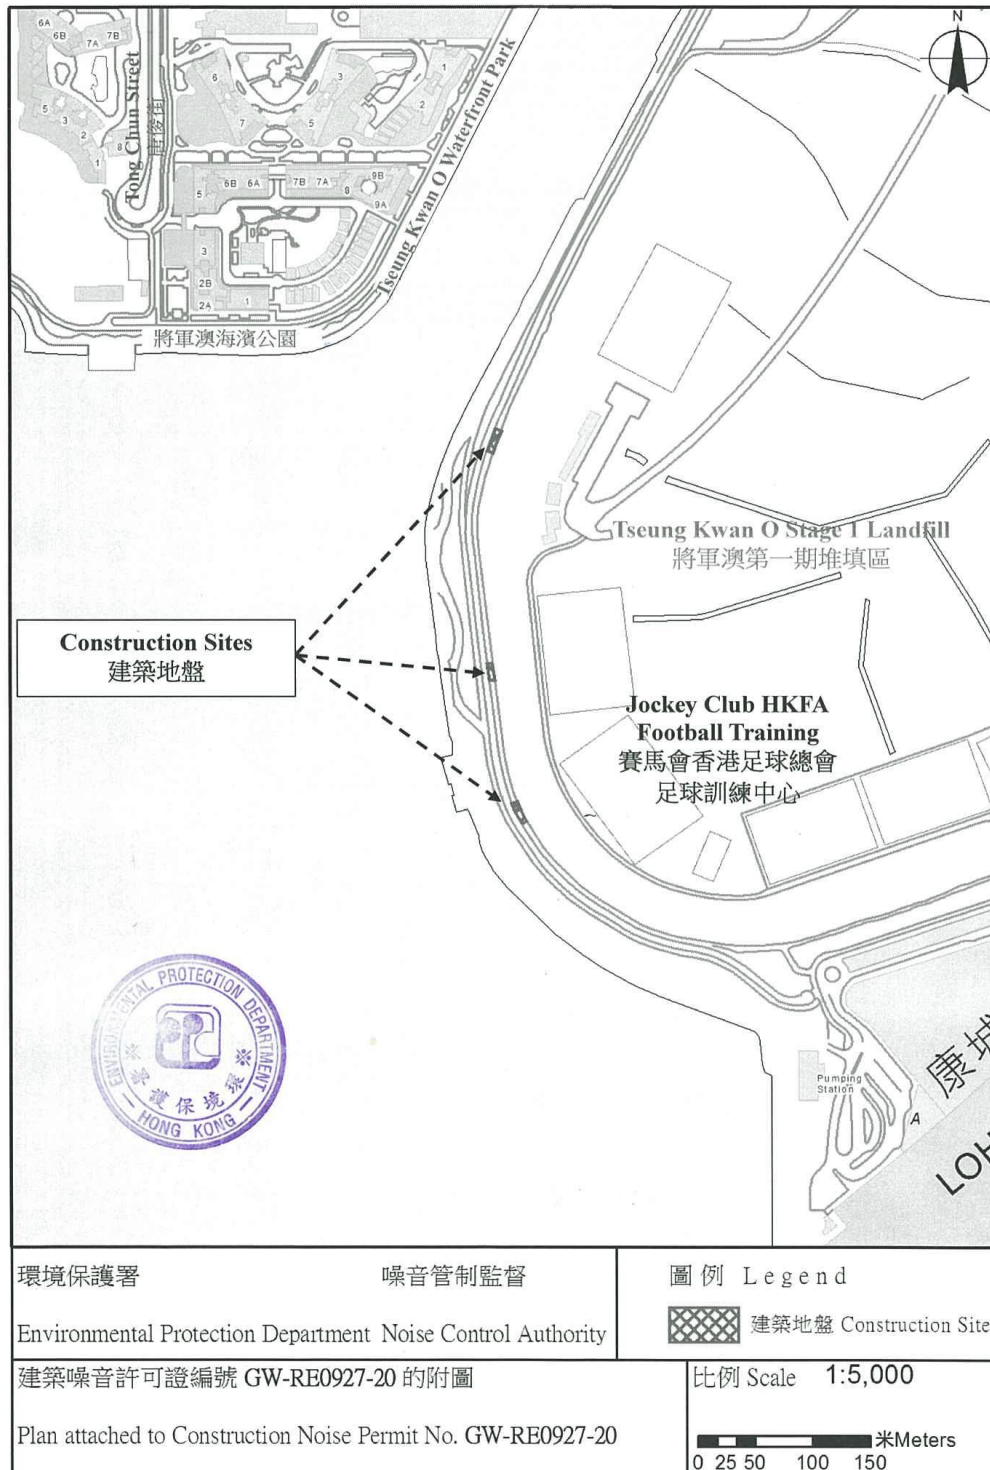

Appendix C: Work Order from WSD showing the work locations



水務署
Water Supplies Department

九龍灣辦事處 Kowloon Bay Office
九龍灣大業里 11 號水務署九龍東區大樓
WSD Kowloon East Regional Building, 11 Tai Yip Lane, Kowloon Bay

By Hand

本署檔號 : (6) in WSD/M/7503/13/WSD/16/M15/300/72 電話 : 2152 5742 /
Our ref. : 3650 3418
來函檔號 : 傳真 : 2351 6949
Your ref. : Fax.

31 August 2020

Penta-Ocean – Concentric Joint Venture
Unit 601, K Wah Centre
191 Java Road, North Point
Hong Kong
(Attn.: Mr. C. C. TIU, Thomas)

Dear Sirs,

**Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O**

**Compensation Event – CE No. 72
Temporary Reinstatement of Deteriorated Grasscrete Road by Bituminous
Pavement along TKO South Waterfront Promenade**

In accordance with NEC Clause 14.3, you are instructed to carry out temporary reinstatement for the deteriorated grasscrete road by bituminous pavement along TKO South Waterfront Promenade as shown on the Drawing No. SK40134/345.

I consider this instruction is a compensation event in accordance with NEC Clause 60.1(1). Please submit a quotation for our consideration pursuant to NEC Clause 61.1.

Yours faithfully,


(Y. H. WONG)
Engineer/Construction (5)
Water Supplies Department

Encl. (w/ SK40134/345)

c.c. Meinhardt Infrastructure and Environment Ltd (Attn.: Mr. K W LEE – by fax: 2540 1580)

Internal: SE/C(3), E/C(7), E/C(10), SQS, SWI/C(10), WI/C(7), AWI/C(10), AWI/C(7) via email



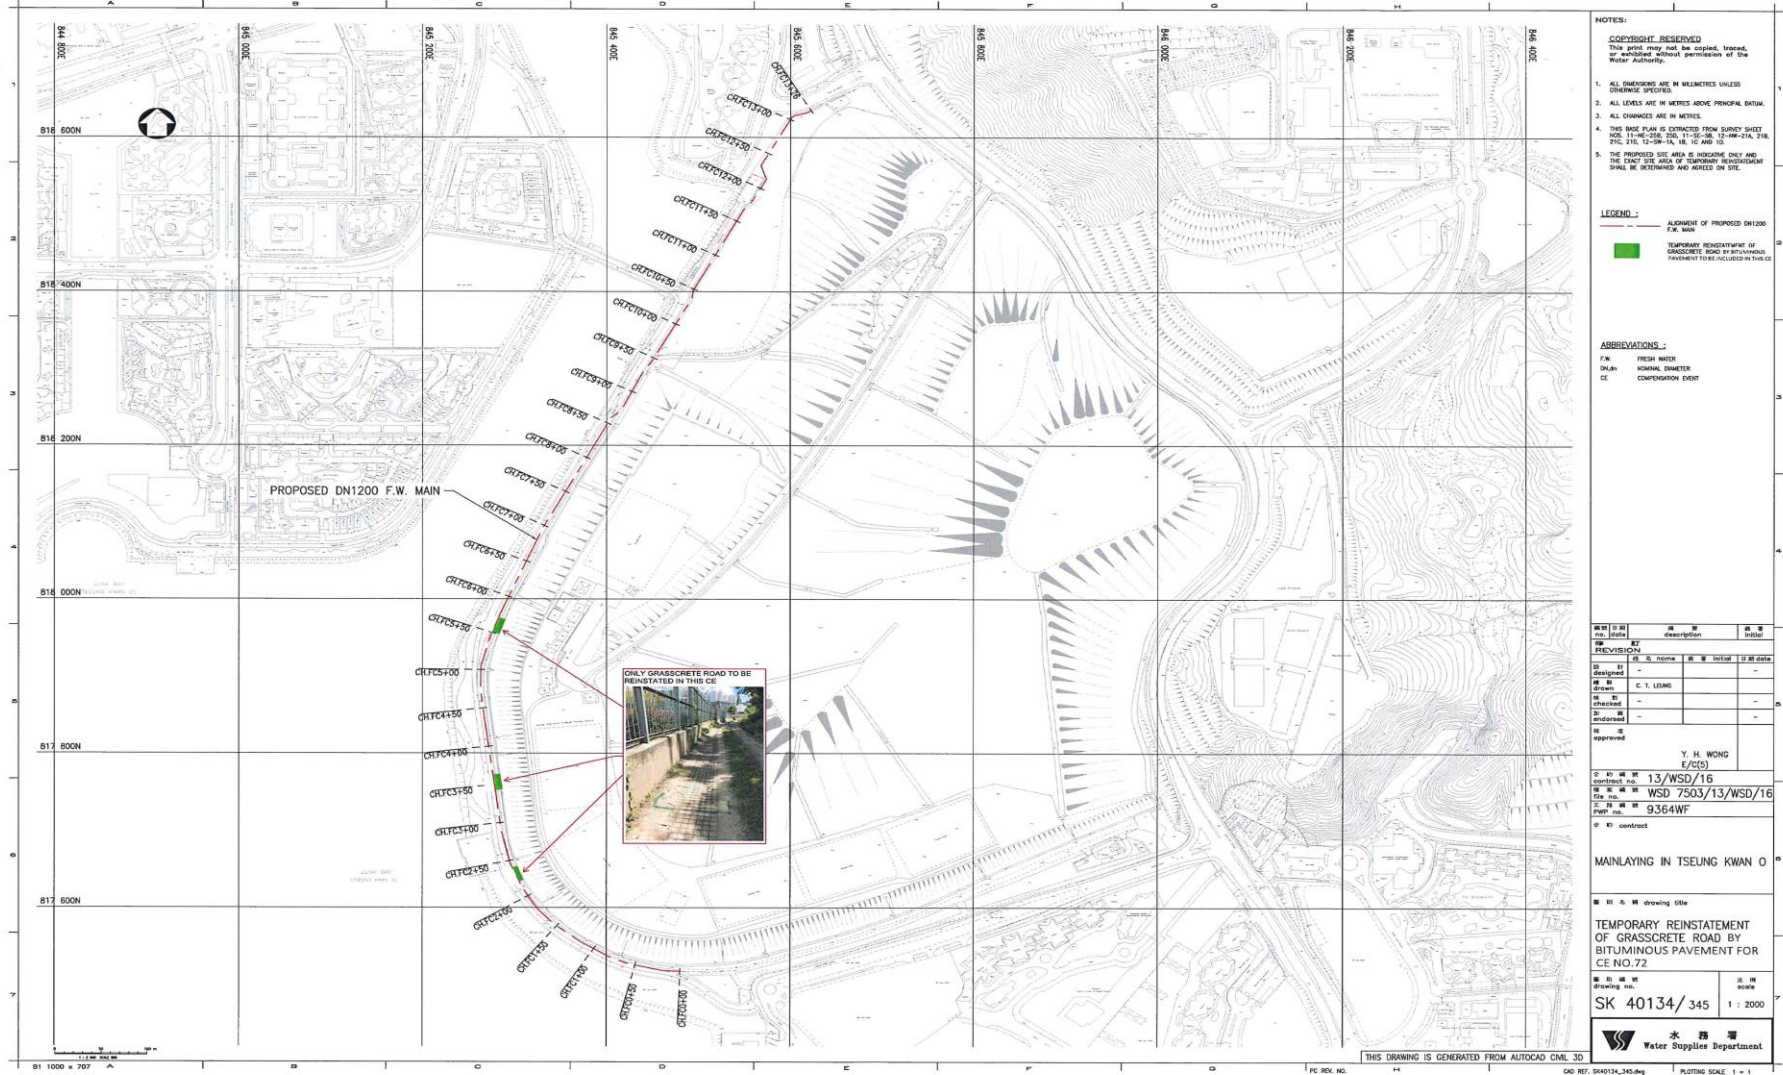

NOTES:
COPYRIGHT RESERVED
 This print may not be copied, traced, or published without permission of the Water Authority.

1. ALL DIMENSIONS ARE IN MILLIMETRES UNLESS OTHERWISE SPECIFIED.
2. ALL LEVELS ARE IN METRES ABOVE PRINCIPAL DATUM.
3. ALL CHANGES ARE IN METRES.
4. THE BORE PLAN IS EXTRACTED FROM CIVIL/307 SHEET NOS. 11-14E-208, 209, 11-15E-302, 303, 304, 305, 12-10P-21A, 21B, 21C, 21D, 12-10P-1A, 1B, 1C AND 1D.
5. THE PROPOSED SITE AREA IS INDICATIVE ONLY AND THE ONLY SET AREA OF TOLERANCE REQUIREMENT SHALL BE DETERMINED AND AGREED ON SITE.

LEGEND:
 --- ALIGNMENT OF PROPOSED DN1200 F.W. MAIN
 ■ TEMPORARY REINSTATEMENT OF GRASSCRETE ROAD BY BITUMINOUS PAVEMENT TO BE INCLUDED IN THIS CE

ABBREVIATIONS:
 F.W. FRESH WATER
 DN=mm NOMINAL DIAMETER
 CE COMPLETION EXIST

項目	姓名	職銜	日期
REVISION	DESCRIPTION	DATE	
1	AS DRAWN		
2	DESIGNED		
3	DRAWN	C. T. LEUNG	
4	CHECKED		
5	ENDORSED		
6	APPROVED		

Y. H. WONG
 13/WSD/16
 contract no. 13/WSD/16
 title no. WSD 7503/13/WSD/16
 PWP no. 9364WF

MAINLAYING IN TSEUNG KWAN O

TEMPORARY REINSTATEMENT OF GRASSCRETE ROAD BY BITUMINOUS PAVEMENT FOR CE NO. 72

SK 40134/345 1:2000

Water Supplies Department
