



Water Supplies Department  
New Works Branch  
Construction Division  
11 Tai Yip Lane  
Kowloon Bay  
Kowloon  
Hong Kong

Your reference:

Our reference: HKWSD201/50/107105

Date: 16 February 2021

Attention: Mr Y M Chan

**BY POST**

Quotation No.: WQ/17/A071  
Independent Environmental Checker for Water Supplies Department  
– Proposed Desalination Plant in TKO Area 137 for Contract No. 13/WSD/16  
Verification of Monthly EM&A Report No. 30

We refer to emails of 11 and 16 February 2021 attaching Monthly EM&A Report No. 30 for the captioned project prepared by the ET.

We have no comment and hereby verify the Monthly EM&A Report No.30 in accordance with Clause 3.5 of the Environmental Permit no. EP-503/2015/A.

Should you have any queries regarding the above, please do not hesitate to contact the undersigned or our Mr Louis Kwan 2618 2831.

Yours faithfully  
ANEWR CONSULTING LIMITED

James Choi  
Independent Environmental Checker

CPSJ/KSYL/CYYR/lsm



**ACUITY**  
SUSTAINABILITY  
CONSULTING LIMITED



Website: [www.acuityhk.com](http://www.acuityhk.com)



Unit C, 11/F, Ford Glory Plaza,  
Nos. 37-39 Wing Hong Street,  
Cheung Sha Wan, Kowloon.



Tel. : (852) 2698 6833  
Fax.: (852) 2698 9383



水務署

Water Supplies Department



**Contract No. 13/WSD/16**

**Mainlaying in Tseung Kwan O**

**Monthly EM&A Report No. 30**  
**(Period from 1 to 31 January 2021)**

February 2021

(Rev. 0)

	<b>Prepared by:</b>	<b>Certified by:</b>
<b>Name</b>	Karen Cheung	Jacky Leung
<b>Position</b>	Environmental Team	Environmental Team Leader
<b>Signature</b>		
<b>Date:</b>	10/02/2021	10/02/2021

## Revision History

<b>0</b>	1 <sup>st</sup> Submission	10 Feb 2021
<b>Rev.</b>	<b>DESCRIPTION OF MODIFICATION</b>	<b>DATE</b>

## CONTENT

<b>Executive Summary</b>	
1.	Basic Project Information ..... 8
2.	Noise Monitoring..... 12
3.	Waste management ..... 17
4.	Landfill gas monitoring ..... 18
5.	Summary of Monitoring Exceedance, Complaints, Notification of Summons and Prosecutions ..... 34
6.	EM&A Site Inspection ..... 35
7.	Future Key Issues ..... 38
8.	Conclusion and Recommendations..... 40

Appendix A	Construction Programme
Appendix B	Overview of Mainlaying in Tseung Kwan O
Appendix C	Summary of Implementation Status of Environmental Mitigation
Appendix D	Impact Monitoring Schedule of the Reporting Month
Appendix E	Noise Monitoring Equipment Calibration Certificate
Appendix F	Event/Action Plan for Noise Exceedance
Appendix G	Noise Monitoring Data
Appendix H	Waste Flow Table
Appendix I	Landfill Gas Monitoring Equipment Calibration Certificate
Appendix J	Landfill Gas Monitoring Data
Appendix K	Complaint Log and Regulatory Compliance Proforma
Appendix L	Site Inspection Proforma
Appendix M	Proactive Environmental Protection Proforma
Appendix N	Impact Monitoring Schedule of Next Reporting Month
Appendix O	Academic Calendar(s)

## EXECUTIVE SUMMARY

### Introduction

- A1. Penta-Ocean - Concentric Joint Venture (POCJV) is contracted to carry out the Mainlaying in Tseung Kwan O under Contract No. 13/WSD/16 (hereinafter known as “the Project”).
- A2. In accordance with the Environmental Monitoring and Audit (EM&A) Manual for the Project, EM&A works should be carried out by Environmental Team (ET), Acuity Sustainability Consulting Limited (ASCL), during the construction phase of the Project.
- A3. This is the 30<sup>th</sup> Monthly EM&A Report, prepared by ASCL, for the Project summarizing the monitoring results and audit findings of the EM&A programme at and around Tseung Kwan O (TKO) during the reporting period from 1 January 2021 to 31 January 2021.
- A4. The EM&A programme for this contract has covered environmental monitoring on construction noise level at selected NSRs and Contractor’s environmental performance auditing in the aspects of construction dust, construction noise, water quality, waste management, Landscape and Visual and Ecology.

### Summary of Main Works Undertaken & Key Mitigation Measures Implemented

- A5. Key works carried out in this reporting period for the Project included the followings:

Location	Location	Works Conducted in the reporting month
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> <li>Hydrostatic pressure testing for completed MS1200 pipeline section.</li> </ul>
	TKO 137 Pit A	<ul style="list-style-type: none"> <li>Pipe trench excavation and ELS works were completed.</li> </ul>
	TKO 137 Pit C	<ul style="list-style-type: none"> <li>Excavation and ELS works for trenchless pit.</li> </ul>
Portion J of the Project Site	Wan Po Rd – Workfront 1	<ul style="list-style-type: none"> <li>Pipe trench excavation and pipe laying were in-progress.</li> </ul>
	Wan Po Rd – Workfront 2	<ul style="list-style-type: none"> <li>Pipe trench excavation and pipe laying were in-progress.</li> </ul>
	Wan Po Rd – Workfront 3	<ul style="list-style-type: none"> <li>Pipe trench excavation and pipe laying were in-progress.</li> </ul>
	Wan Po Rd – Pit A	<ul style="list-style-type: none"> <li>Pit excavation and ELS works.</li> </ul>
	Wan Po Rd – Pit B	<ul style="list-style-type: none"> <li>Pit excavation and ELS works.</li> </ul>
	Landfill Stage 1 – Area A	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying were conducted.</li> </ul>
	Landfill Stage 1 – Area B	<ul style="list-style-type: none"> <li>Trench reinstatement works.</li> </ul>
Cycle Track – Workfront 1	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying were in-progress.</li> </ul>	

Location	Location	Works Conducted in the reporting month
	Cycle Track – Workfront 2	• Trench excavation and pipe laying were in-progress.
	Velodrome – Pit L	• Excavation and ELS works were completed.
	Velodrome – Pit M	• Pipe jacking works were conducted.
	Velodrome – Pit O	• Establishment for pipe jacking works
	Velodrome – Pit P	• Pit excavation and ELS works were completed.
	Mau Wu Tsai – Workfront 1	• Trench excavation and pipe laying works were conducted.
	Mau Wu Tsai – Workfront 2	• Trench excavation and pipe laying works were conducted.

A6. The major environmental impacts brought by the above construction works include:

- Construction dust and noise generation of saw cutting of concrete surface, mainlaying of pipes, hole-drilling, excavation works and installation works.
- Waste generation from the construction activities

A7. The key environmental mitigation measures implemented for the Project in this reporting period associated with the above construction works include:

- Construction dust and noise generation of saw cutting of concrete surface, mainlaying of pipes, hole-drilling, excavation works and installation works
- Reduction of noise from equipment and machinery on-site
- Sorting and storage of general refuse and construction waste

#### **Summary of Exceedance & Investigation & Follow-up**

A8. Noise monitoring was conducted in the reporting month for NSR4 Creative Secondary School on 8, 13, 21 and 27 January 2021 as construction works were conducted within 300m to the noise sensitive receiver. No project-related exceedance of the Action and Limit Level was recorded during the reporting period.

A9. The Education Bureau (EDB) has announced that all kindergartens as well as primary and secondary schools (including special schools and schools offering non-local curriculum) will continue to suspend face to face classes and school activities until the beginning of school's Chinese New Year holidays due to the spread of the Novel Coronavirus. Hence the noise limit level will be 70.0 dB(A). Further information and Academic School Calendar can be found in Appendix O.

**Complaint Handling and Prosecution**

- A10. No project-related environmental complaint was received during the reporting period.
- A11. Neither notifications of summons nor prosecution was received for the Project.

**Reporting Change**

- A12. There were no changes reported that may affect the on-going EM&A programme.

**Summary of Upcoming Key Issues and Key Mitigation Measures**

- A13. Key works in February 2021 (the next reporting month) for the Project will include the followings:

Location	Location	Forecast Works for January 2021
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> <li>Hydrostatic pressure testing for completed MS1200 pipeline section will be conducted.</li> </ul>
	TKO 137 Pit B	<ul style="list-style-type: none"> <li>Pipe jacking works will be commenced.</li> </ul>
	TKO 137 Pit C	<ul style="list-style-type: none"> <li>Pit excavation and ELS works will be continued.</li> </ul>
Portion J of the Project Site	Wan Po Rd – Workfront 1	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying will be conducted.</li> </ul>
	Wan Po Rd – Workfront 2	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying works will be conducted.</li> <li>Trial pit works for Pit 1 will be commenced.</li> </ul>
	Wan Po Rd – Workfront 3	<ul style="list-style-type: none"> <li>Trench excavation and mainlaying works will be conducted.</li> </ul>
	Wan Po Rd – Pit A	<ul style="list-style-type: none"> <li>Excavation and ELS works will be conducted.</li> </ul>
	Wan Po Rd – Pit B	<ul style="list-style-type: none"> <li>Excavation and ELS works will be conducted.</li> </ul>
	Landfill Stage 1 – Area A	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying works will be conducted.</li> </ul>
	Landfill Stage 1 – Area B	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying works will be conducted.</li> </ul>
	Cycle Track – Workfront 1	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying works will be conducted.</li> </ul>
	Cycle Track – Workfront 2	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying works will be conducted.</li> </ul>
	Velodrome – Pit K	<ul style="list-style-type: none"> <li>Trenchless pit for hand-shield works will be conducted</li> </ul>
	Velodrome – Pit L	<ul style="list-style-type: none"> <li>Trenchless pit for hand-shield works will be conducted</li> </ul>

<b>Location</b>	<b>Location</b>	<b>Forecast Works for January 2021</b>
	Velodrome – Pit M	• Pipe jacking works will be continued.
	Velodrome – Pit O	• Pipe jacking works will be continued.
	Mau Wu Tsai – Workfront 1	• Trench excavation and pipe mainlaying works will be conducted.
	Mau Wu Tsai – Workfront 2	• Trench excavation and pipe mainlaying works will be conducted

A14. The major environmental impacts brought by the above construction works will include:

- Construction dust and noise generation of saw cutting of concrete surface, mainlaying of pipes, pipe piling, excavation works and ELS works.
- Waste generation from construction activities

A15. The key environmental mitigation measures for the Project in the coming reporting period associated with the above construction works will include:

- Construction dust and noise generation of saw cutting of concrete surface, mainlaying of pipes, pipe piling, excavation works and ELS works.
- Reduction of noise from equipment and machinery on-site
- Sorting and storage of general refuse and construction waste



## 1. BASIC PROJECT INFORMATION

### 1.1 Background

The proposed Desalination Plant at Tseung Kwan O (DPTKO) will produce potable water with an initial capacity of 135 million liters per day (MLD), expandable to an ultimate capacity of 270 MLD in the future to provide a secure and alternative fresh water resource complying with the World Health Organization (WHO) standards. The plant will adopt the Seawater Reverse Osmosis (SWRO) technology, which dominates the market due to its reliability and progressive reduction in cost as the technology advances.

Pursuant to the Environmental Impact Assessment Ordinance (EIAO), the Director of Environmental Protection granted the Variation of Environmental Permit (No. EP-503/2015/A) to Water Supplies Department (WSD) for the Project on 26 January 2018.

The scope of the Contract may be considered in brief, to consist of the laying of about 10km long 1200mm diameter fresh water mains and the associated works along the alignment of the Project as shown with the overall view in **Appendix B**.

### 1.2 The Reporting Scope

This is the 30<sup>th</sup> Monthly EM&A Report for the Project which summarizes the key findings of the EM&A programme during the reporting period from 1 January 2021 to 31 January 2021.

### 1.3 Project Organization

The Project Organization structure for Construction Phase is presented in **Figure 1.1**.

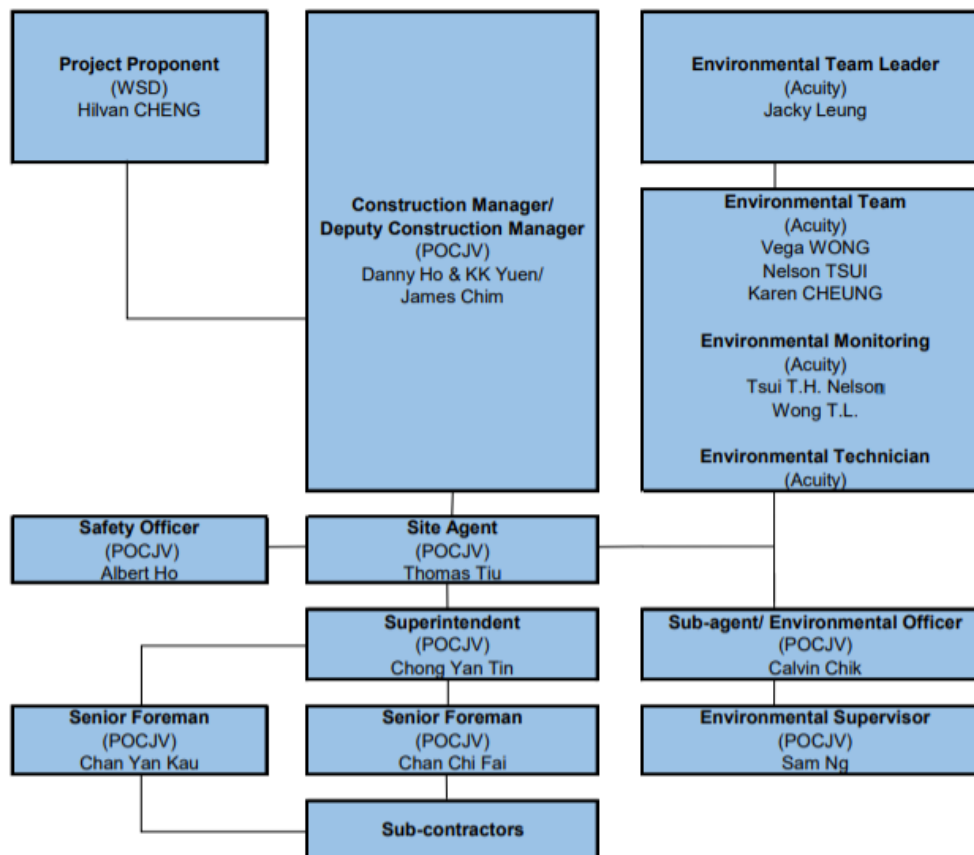


Figure 1.1 Project Organization Chart

Contact details of the key personnel are presented in **Table 1.1** below:

Party	Position	Name	Telephone no.
Penta-Ocean Concentric Joint Venture	Environmental Officer	Calvin Chik	9863 5630
Acuity Sustainability Consulting Limited	Environmental Team Leader	Jacky Leung	2698 6833
ANewR Consulting Limited	Independent Environmental Checker	James Choi	2618 2831

#### 1.4 Summary of Construction Works

Details of the major construction works undertaken in this reporting period are shown in **Table 1.2** and the construction works locations are shown in **Appendix B**. The construction programme is presented in **Appendix A**.

**Table 1.2 Summary of the Construction Works Undertaken during the Reporting Month**

Progress of work activities (Completed)		
Location	Location	Works Conducted in the reporting month
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> <li>Backfilling and reinstatement works were completed at pipe end.</li> </ul>
	TKO 137 Pit A	<ul style="list-style-type: none"> <li>Pit excavation and ELS works were completed.</li> </ul>
Portion J of the Project Site	Velodrome – Pit L	<ul style="list-style-type: none"> <li>Pit excavation and ELS works were completed.</li> </ul>
	Velodrome – Pit P	<ul style="list-style-type: none"> <li>Pit excavation and ELS works were completed.</li> </ul>

Progress of work activities (In Progress)		
Location	Location	Works Conducted in the reporting month
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> <li>Hydrostatic pressure testing for completed MS1200 pipeline section.</li> </ul>
	TKO 137 Pit C	<ul style="list-style-type: none"> <li>Pit excavation and ELS works.</li> </ul>
Portion J of the Project Site	Wan Po Rd – Workfront 1	<ul style="list-style-type: none"> <li>Pipe trench excavation and pipe laying were in-progress.</li> </ul>
	Wan Po Rd – Workfront 2	<ul style="list-style-type: none"> <li>Pipe trench excavation and pipe laying were in-progress.</li> </ul>
	Wan Po Rd – Workfront 3	<ul style="list-style-type: none"> <li>Pipe trench excavation and pipe laying were in-progress.</li> </ul>
	Wan Po Rd – Pit A	<ul style="list-style-type: none"> <li>Pit excavation and ELS works.</li> </ul>
	Wan Po Rd – Pit B	<ul style="list-style-type: none"> <li>Pit excavation and ELS works.</li> </ul>
	Landfill Stage 1 – Area A	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying were conducted.</li> </ul>
	Landfill Stage 1 – Area B	<ul style="list-style-type: none"> <li>Trench reinstatement works were conducted.</li> </ul>
	Cycle Track – Workfront 1	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying were in-progress.</li> </ul>
	Cycle Track – Workfront 2	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying were in-progress.</li> </ul>
	Velodrome – Pit M	<ul style="list-style-type: none"> <li>Pipe jacking works were in-progress.</li> </ul>
	Velodrome – Pit O	<ul style="list-style-type: none"> <li>Establishment for pipe jacking works was in-progress.</li> </ul>
	Mau Wu Tsai – Workfront 1	<ul style="list-style-type: none"> <li>Pipe laying and trench excavation.</li> </ul>
Mau Wu Tsai – Workfront 2	<ul style="list-style-type: none"> <li>Pipe laying and trench excavation.</li> </ul>	

### 1.5 Summary of Environmental Status

A summary of the valid permits, licences, and or notifications on environmental protection for this Project is presented in **Table 1.3**.

**Table 1.3 Summary of the Status of Valid Environmental Licence, Notification, Permit and Documentations**

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Variation of Environmental Permit	EP no.: EP-503/2015/A	Throughout the Contract	-
Notification of Construction Works under the Air Pollution Control (Construction Dust) Regulation (Form NA)	Ref no.: 423775	Throughout the Contract	-
Chemical Waste Producer Registration	WPN: 5213-839-P3287-01	Throughout the Contract	-
Billing Account for Disposal of Construction Waste	A/C no.: 7029491	Throughout the Contract	-
Water Discharge Licence	WT00032336-2018	Until 31 Dec 2023	-
Construction Noise Permit	GW-RE0846-20	Until 31 Mar 2021	-
Construction Noise Permit (Hong Kong Velodrome)	GW-RE0961-20	Until May 2021	-
Construction Noise Permit (Landfill Stage 1 near Jockey Club HKFA Football Training Centre)	GW-RE0927-20	Until 24 Jan 2021	-

The status for all environmental aspects is presented **Table 1.4**.

**Table 1.4 Summary of Status for Key Environmental Aspects under the EM&A Manual**

Parameters	Status
Noise	
Baseline Monitoring	The baseline noise monitoring result has been reported in Baseline Monitoring Report and submitted to EPD under VEP Condition 3.4.
Impact Monitoring	On-going
Waste Management	
Mitigation Measures in Waste Monitoring Plan	On-going
Landfill Gas	
Impact Monitoring	On-going
Environmental Audit	
Site Inspection	On-going

Other than the EM&A works by ET, regular environmental management meetings were conducted in order to enhance environmental awareness and closely monitor the environmental performance of the contractors.

The EM&A programme has been implemented in accordance with the recommendations presented in the approved EIA Report and the EM&A Manual. A summary of implementation status of the environmental mitigation measures for the construction phase of the Project during the reporting period

is provided in **Appendix C**.

## 2. NOISE MONITORING

### 2.1 Monitoring Requirements

To ensure no adverse noise impact, noise monitoring is recommended to be carried out within 300m radius from the nearby noise sensitive receivers (NSRs), during construction phase. The NSRs selected as monitoring station are (i) NSR4 – Creative Secondary School, (ii) NSR24 – PLK Laws Foundation College, and (iii) NSR31 – School of Continuing and Professional Studies – CUHK respectively.

In accordance with the EM&A Manual, baseline noise level at the noise monitoring stations were established as presented in the Baseline Monitoring Report. Impact noise monitoring will be conducted once per week in the form of 30-minute measurements Leq, L10 and L90 levels recorded at each monitoring station between 0700 and 1900 on normal weekdays.

Referring to EM&A manual Section 4.1.2, the impact noise monitoring should be carried out at all the designated monitoring stations when there are project-related construction activities undertaken within a radius of 300m from the monitoring stations.

Impact monitoring for noise impact was conducted in the reporting month for NSR4 – Creative Secondary School on 8, 13, 21 and 27 January 2021 as construction works were conducted within 300m to the noise sensitive receiver. Detailed monitoring results can be found in **Appendix G**.

The Education Bureau (EDB) has announced that all kindergartens as well as primary and secondary schools (including special schools and schools offering non-local curriculum) will continue to suspend face to face classes and school activities until the beginning of school's Chinese New Year holiday due to the spread of the Novel Coronavirus.. Hence the noise limit level will be 70.0 dB(A). Further information and Academic School Calendar can be found in Appendix O.

### 2.2 Noise Monitoring Parameters, Time, Frequency

Impact noise monitoring was conducted weekly in the reporting period between 0700-1900 on normal weekdays. No construction works were carried out during 1900-0700 in all days or any time on Sundays or general holidays during the reporting period.

Construction noise level measured in terms of the A-weighted equivalent continuous sound pressure level (LAeq). Leq<sub>30min</sub> was used as the monitoring parameter for the time period between 0700 and 1900 on normal weekdays. **Table 2.1** summarizes the monitoring parameters, frequency and duration of

the impact noise monitoring. The monitoring schedule is provided in **Appendix D**.

**Table 2.1 Noise Monitoring Parameters, Time, Frequency and Duration**

Time	Frequency	Duration	Parameters
Daytime: 0700-1900	Once per week	Continuously in $L_{eq\ 5min}/L_{eq\ 30min}$ (average of 6 consecutive $L_{eq}$ 5min)	$L_{eq}$ , $L_{10}$ & $L_{90}$

### 2.3 Noise Monitoring Locations


The monitoring locations should normally be made at a point 1m from the exterior of the NSRs building façade and be at a position 1.2m above the ground. A correction of +3dB(A) should be made to the free-field measurements.

According to the environmental findings detailed in the EIA report and Baseline Monitoring Report, the designated locations for the construction noise monitoring are listed in **Table 2.2** below.


**Table 2.2 Noise Monitoring Location**

NSR ID	Noise Sensitive Receivers	Monitoring Location	Position
NSR 4	Creative Secondary School	Roof Floor	1 m from facade
NSR 24	PLK Laws Foundation College	Pedestrian Road on Ground Floor	Free-field
NSR 31	School of Continuing and Professional Studies - CUHK	Roof Floor	1 m from facade


Three noise monitoring locations for impact monitoring at the nearby sensitive receivers are shown in **Figure 2.1-2.3**.

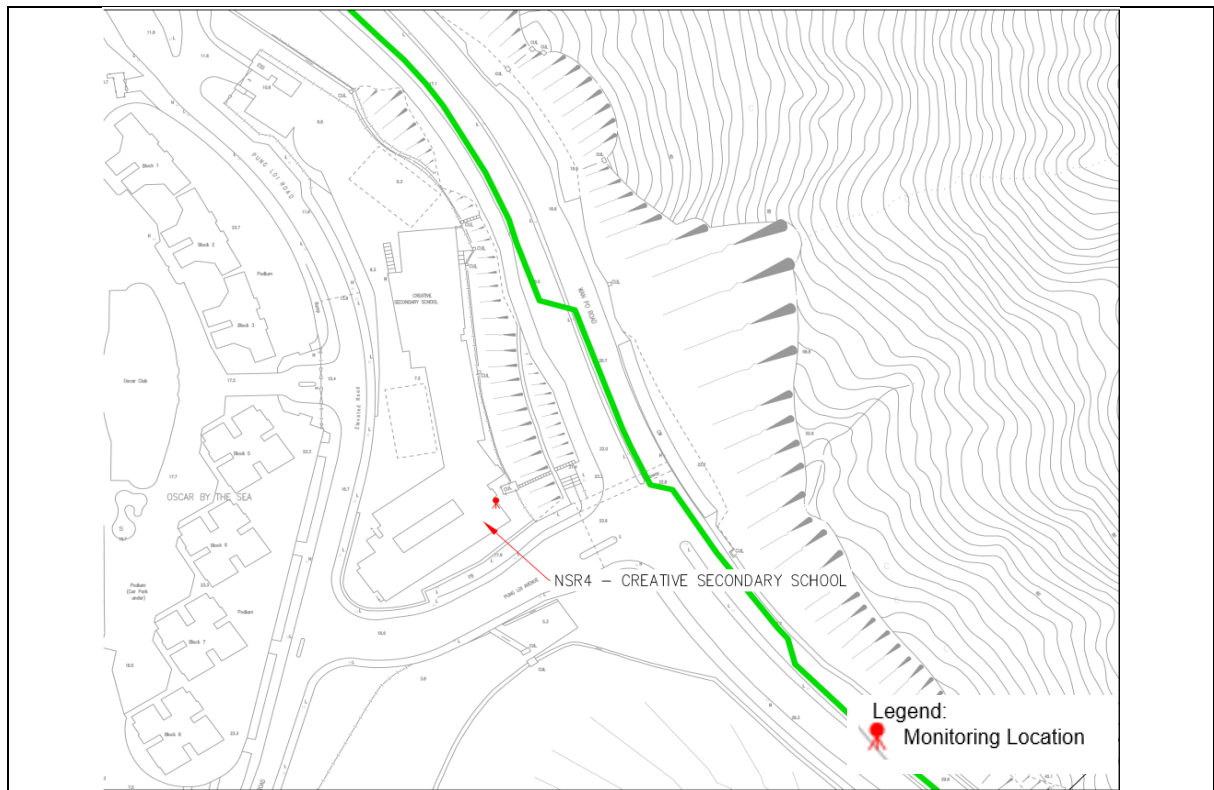

**Figure 2.1 NSR4 Creative Secondary School**

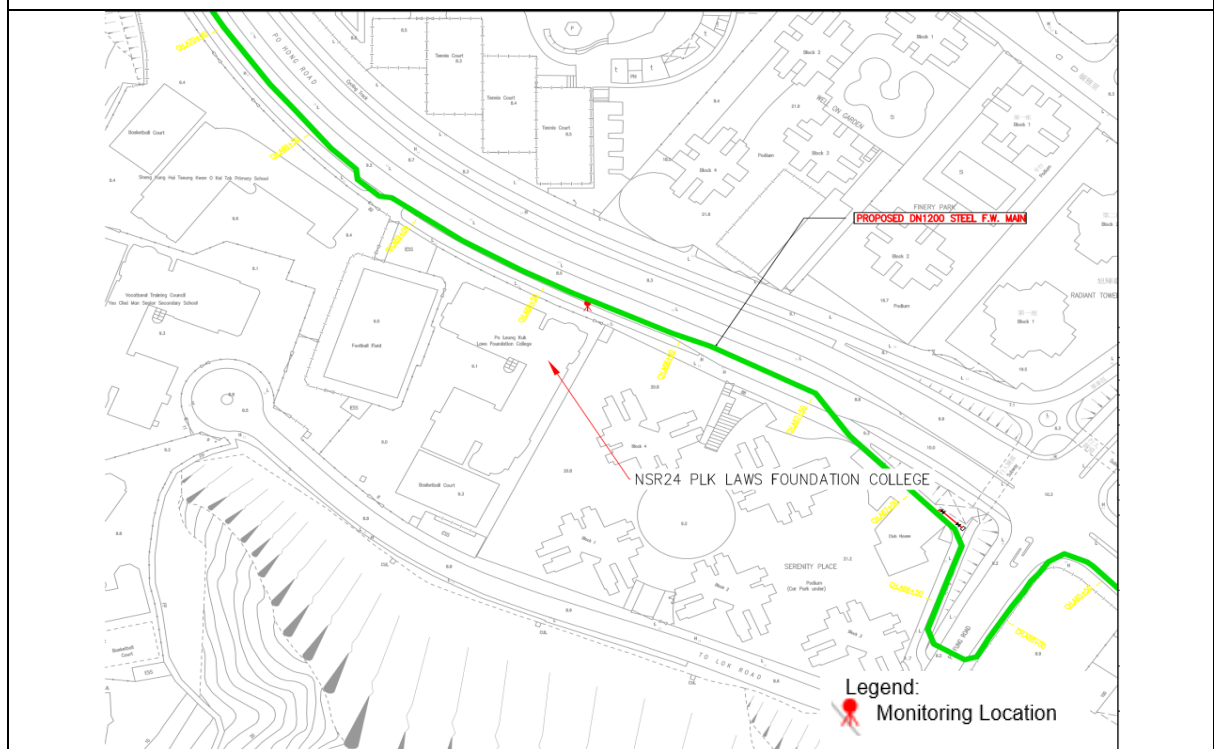

**Figure 2.2 NSR24 PLK Laws Foundation College**

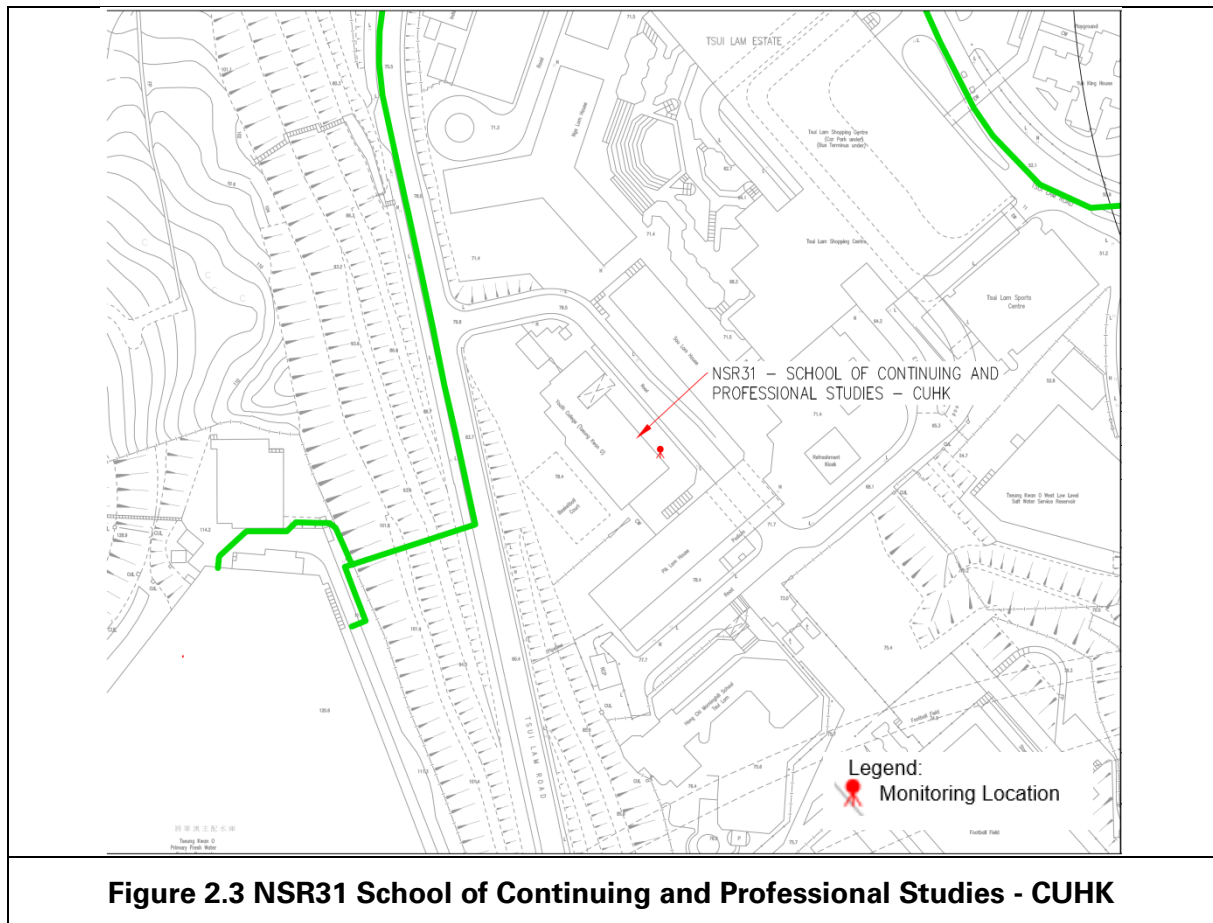

#### 2.4 Impact Monitoring Methodology

Integrated sound level meter shall be used for the noise monitoring. The meter shall be in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level before and after the noise measurements agree to within 1.0 dB(A). Calibration certificates of the instruments used are presented in **Appendix E**. Noise measurements shall not be made in the presence of fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.



Table 2.3 Impact Noise Monitoring Equipment

Equipment	Brand and Model	Serial Number	Date of Calibration	Calibration Certificate Expiry Date	Detection Limit
Sound Level Meter	NTi XL2	A2A-13548-E0	10/01/2020	09/01/2021	30-130 dB(A)
Sound Level Meter	NTi XL2	A2A-13663-E0	09/09/2020	08/09/2021	30-130 dB(A)
Sound Level Meter	Svantek 971	77731	13/02/2020	12/02/2021	34.2-136.2
Sound Level Meter Calibrator	Pulsar 105	63705	06/08/2020	05/08/2021	Nil
Pocket Wind Meter Anemometer	Kestrel 1000 Wind Meter	Nil	Nil	Nil	Nil

## 2.5 Action and Limit Levels

The Action/Limit Levels are in line with the criteria of Practice Note for Professional Persons (ProPECC PN 2/93) "Noise from Construction Activities – Non-statutory Controls" and Technical Memorandum on Environmental Impact Assessment Process issued by HKSAR Environmental Protection Department ["EPD"] under the Environmental Impact Assessment Ordinance, Cap 499, S.16 are presented in **Table 2.4**.

**Table 2.4 Action and Limit Levels for Noise**

Time Period	Action	Limit (dB(A))
0700-1900 on normal weekdays	When one documented complaint is received from any one of the noise sensitive receivers	<ul style="list-style-type: none"> <li>70 dB(A) for school and</li> <li>65 dB(A) during examination period</li> </ul>
Notes: (a) Limits specified in the GW-TM and IND-TM for construction and operation noise, respectively.		

If exceedances were found during noise monitoring, the actions in accordance with the Event and Action Plan shall be carried out according to **Appendix F**.

## 2.6 Monitoring Results and Observations

Referring to EM&A manual Section 4.1.2, impact monitoring for noise impact was conducted in the reporting month for NSR4 – Creative Secondary School on 8, 13, 21 and 27 January 2021.

The Education Bureau (EDB) has announced that all kindergartens as well as primary and secondary schools (including special schools and schools offering non-local curriculum) will continue to suspend face to face classes and school activities until the beginning of school's Chinese New Year holidays due to the

spread of the Novel Coronavirus. Hence the noise limit level will be 70.0 dB(A). Further information and Academic School Calendar can be found in Appendix O.

Detailed monitoring results are presented in **Appendix G**.

### 3. WASTE MANAGEMENT

3.1 The waste generated from this Project includes inert construction and demolition (C&D) materials, and non-inert C&D materials. Non-inert C&D materials are made up of general refuse, vegetative wastes and recyclable wastes such as plastics and paper/cardboard packaging waste. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in **Table 3.1**. Details of cumulative waste management data are presented as a waste flow table in **Appendix H**.

**Table 3.1 Quantities of waste generated from the Project**

Reporting period	Quantity					
	Inert C&D Materials (in '000m <sup>3</sup> )	Chemical Waste (in '000kg)	Non-inert C&D Materials			
			Others, e.g. General Refuse disposed at Landfill (in '000m <sup>3</sup> )	Recycled materials		
				Paper/card board (in '000kg)	Plastics (in '000kg)	Metals (in '000kg)
January-21	2.438	0.000	0.006	0.065	0.000	0.000

## 4. LANDFILL GAS MONITORING

### 4.1 Monitoring Requirement

In accordance with Section 11 of the EM&A Manual, monitoring of landfill gas is required for construction works within the 250m Consultation Zone. Part of the desalination plant and the indicative area of natural slope mitigation works fall within the SENT Landfill Extension Consultation Zone; and part of the 1,200 mm diameter fresh water mains along Wan Po Road falls within the SENT Landfill and SENT Landfill Extension Consultation Zones, TKO Stage II/III Restored Landfill and TKO Stage I Restored Landfill Consultation Zones.

### 4.2 Monitoring Location

Monitoring of oxygen, methane, carbon dioxide and barometric pressure was performed for excavations at 1m depth or more within the consultation Zone. In this reporting period, 698 times of monitoring was recorded.

During construction of works within the consultation zones, excavations of 1m depth or more was monitored:

- At the ground surface before excavation commences;
- Immediately before any worker enters the excavation;
- At the beginning of each working day for the entire period the excavation remains open; and
- Periodically through the working day whilst workers are in the excavation.

For excavations between 300mm and 1m deep, measurements should be carried out:

- Directly after the excavation has been completed; and
- Periodically whilst the excavation remains open.

The area required to be monitored for landfill gas in the reporting period are shown in **Figure 4.1** to **Figure 4.15**.

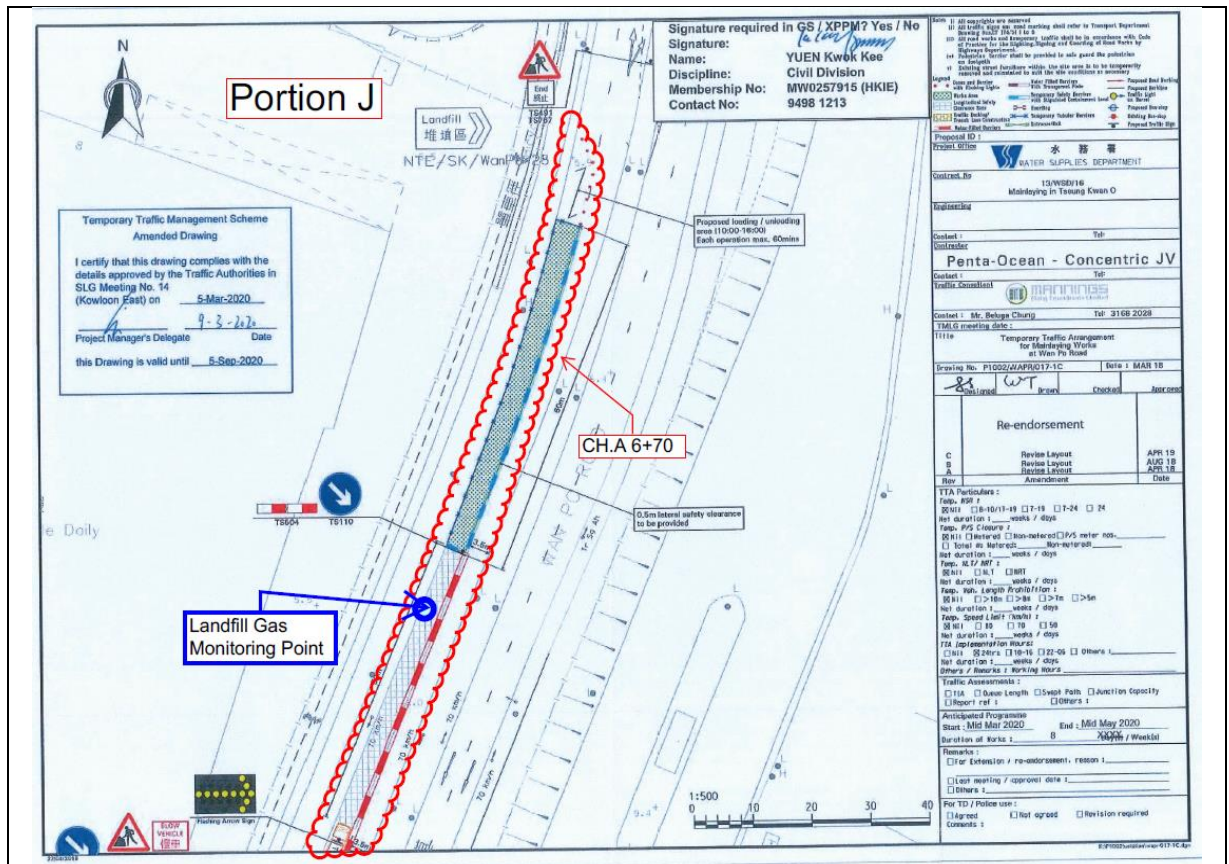


Figure 4.1 Monitoring Location - CH.A 6+70

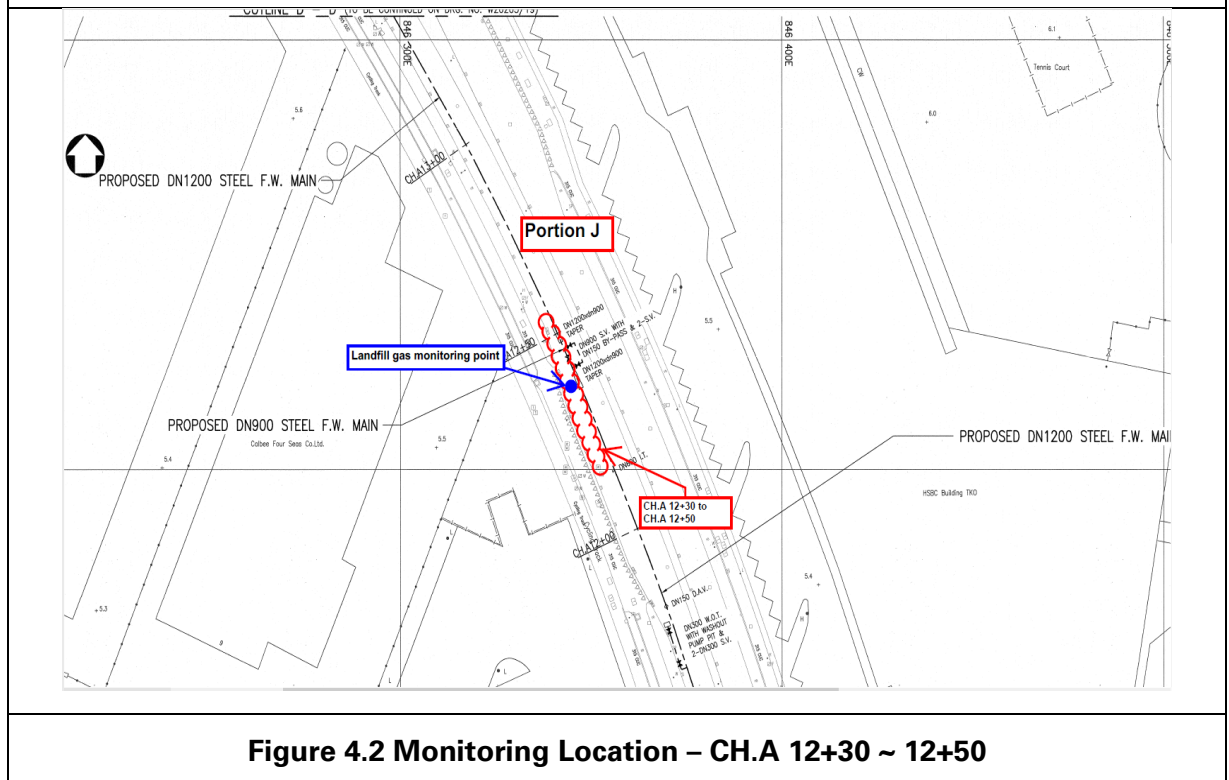


Figure 4.2 Monitoring Location - CH.A 12+30 ~ 12+50

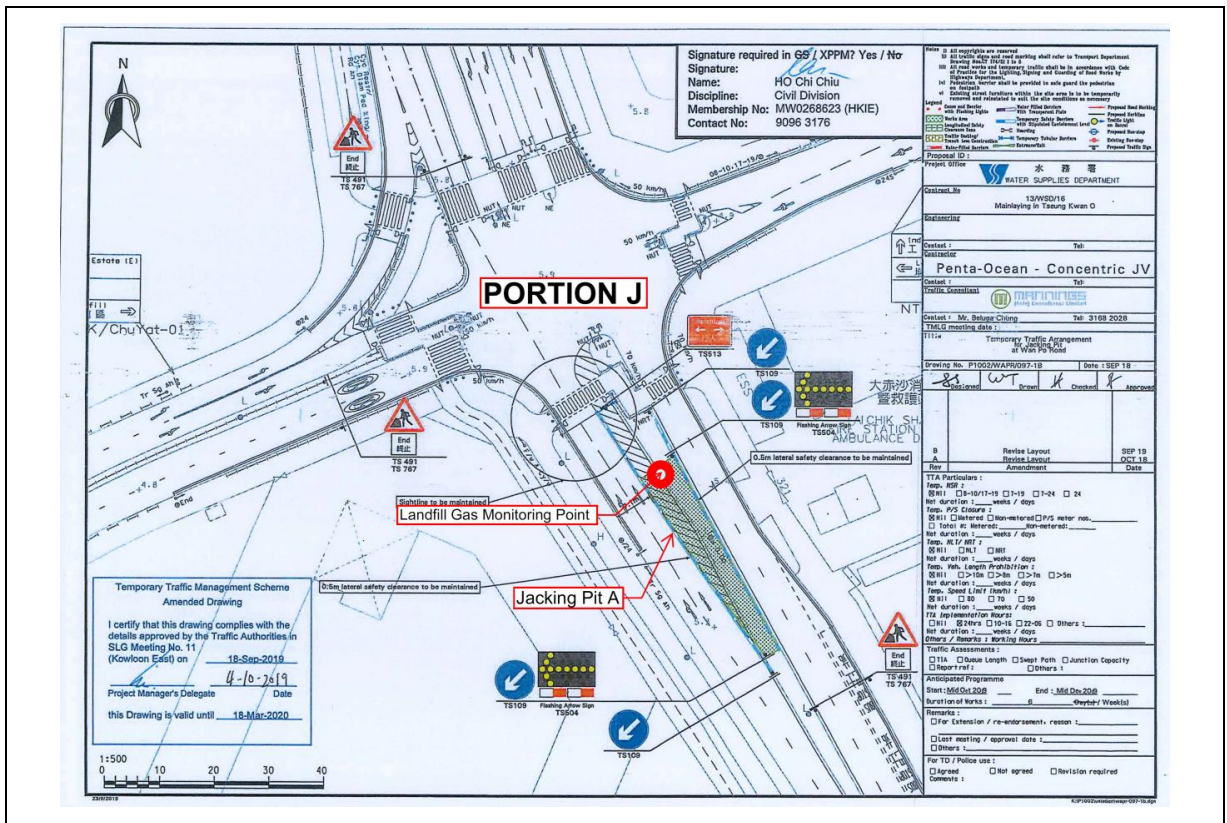


Figure 4.3 Monitoring Location – CH.A 13+50 ~ 14+00 (Pit A)

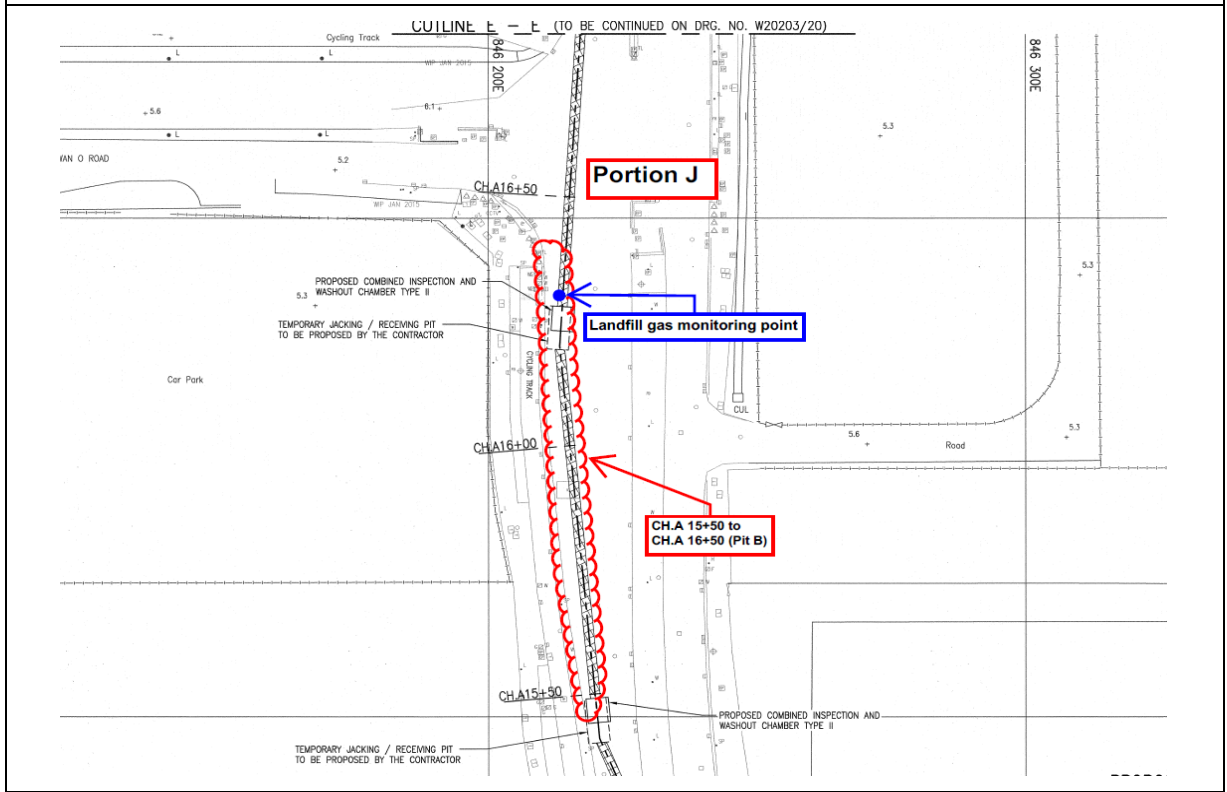


Figure 4.4 Monitoring Location – CH.A 15+50 ~ 16+50 (Jacking Pit B)

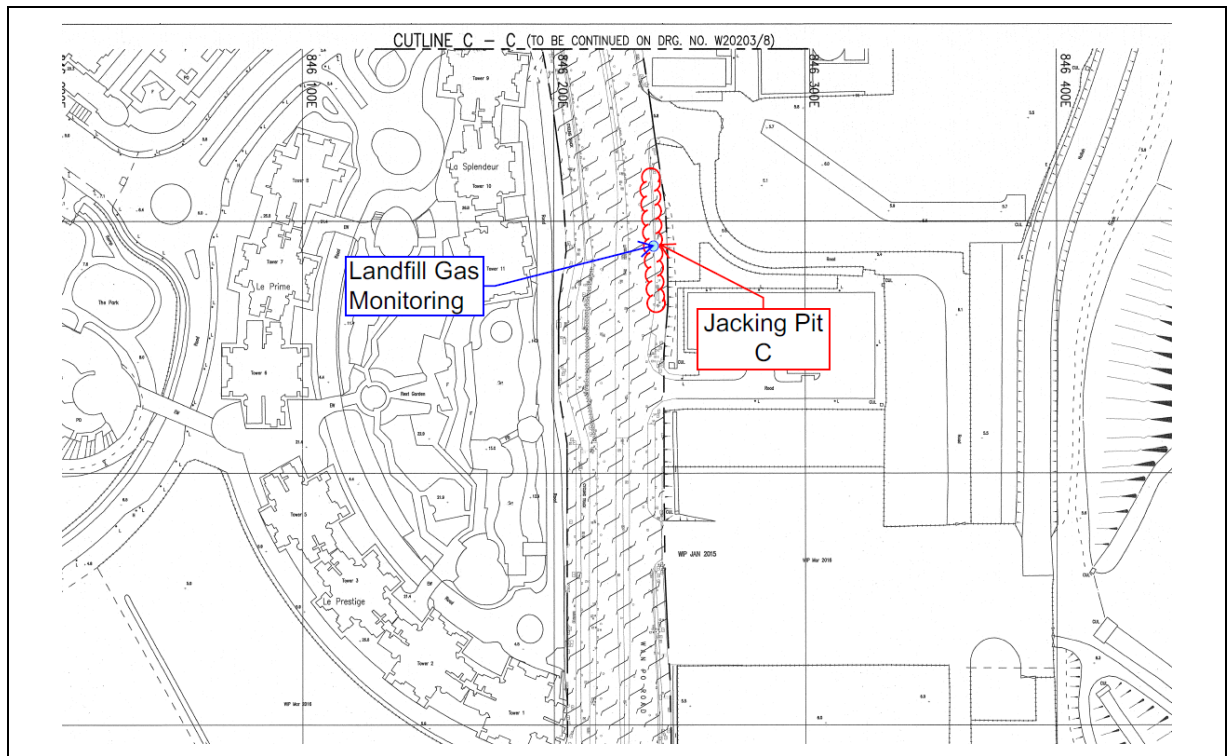


Figure 4.5 Monitoring Location – CH.A 19+15 ~19+50 (Pit C)

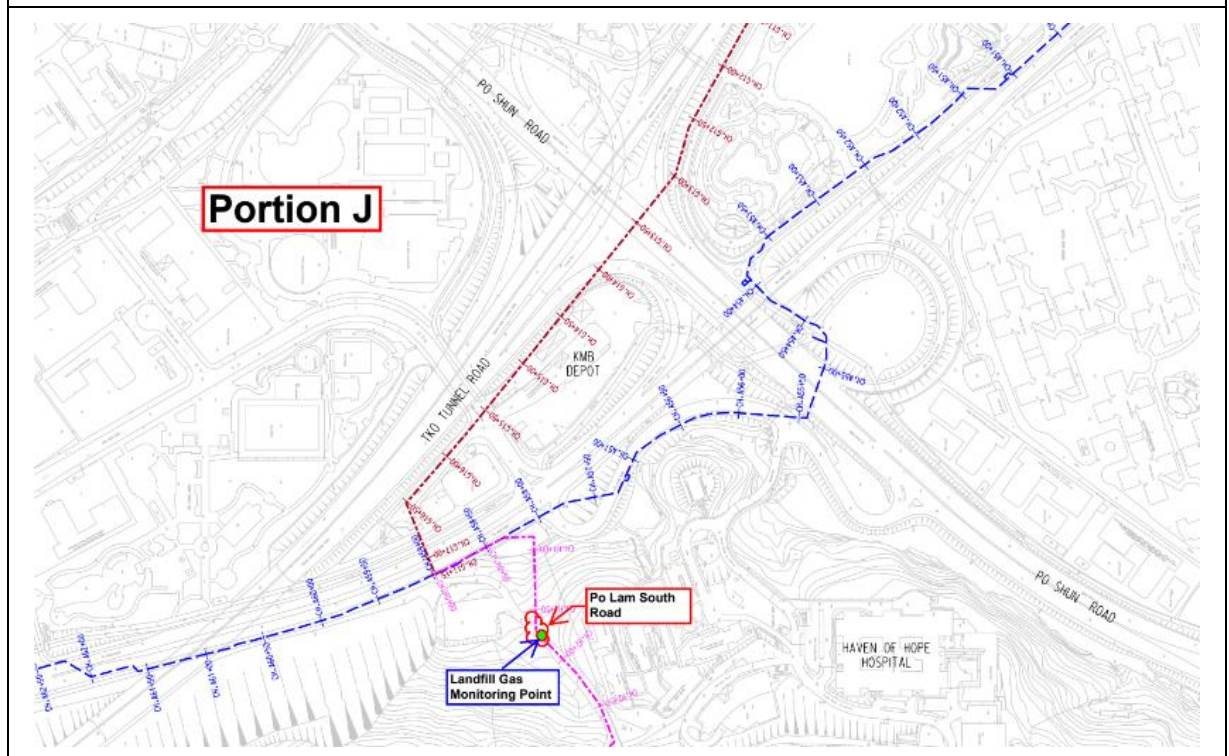


Figure 4.6a Monitoring Location – Mau Wu Tsai 1

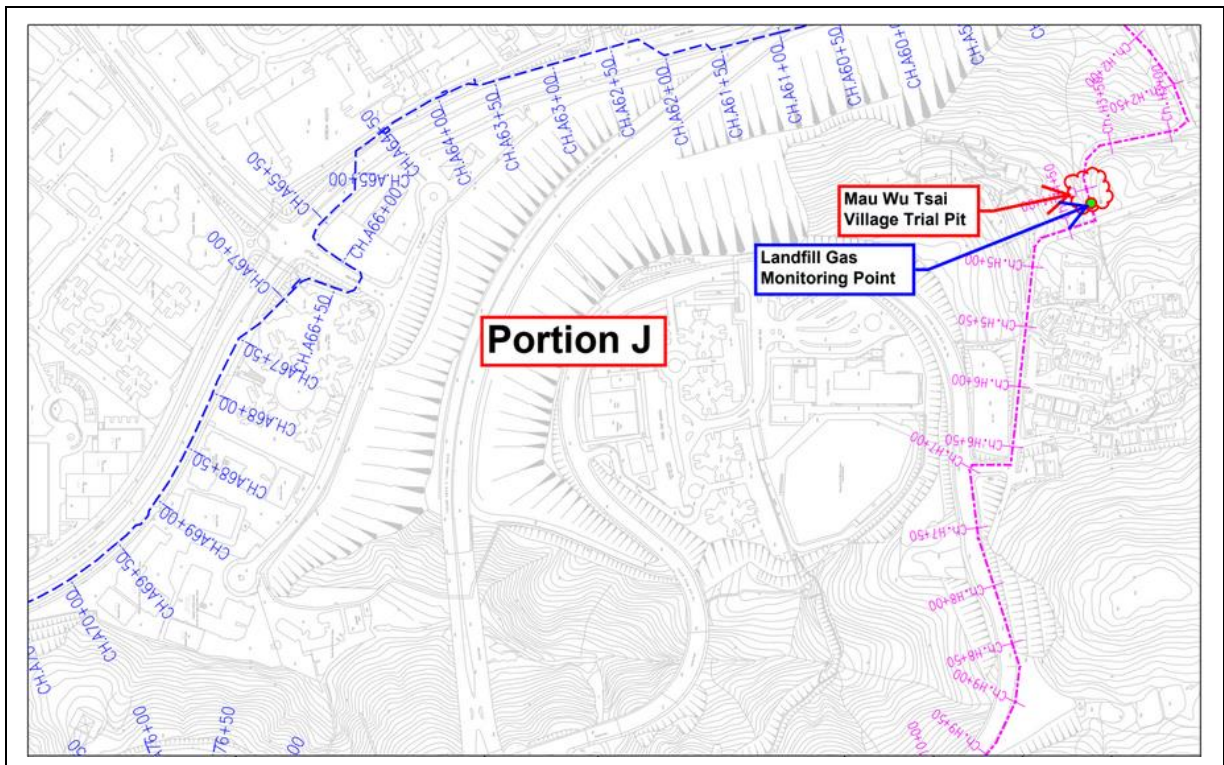


Figure 4.6b Monitoring Location – Mau Wu Tsai 2

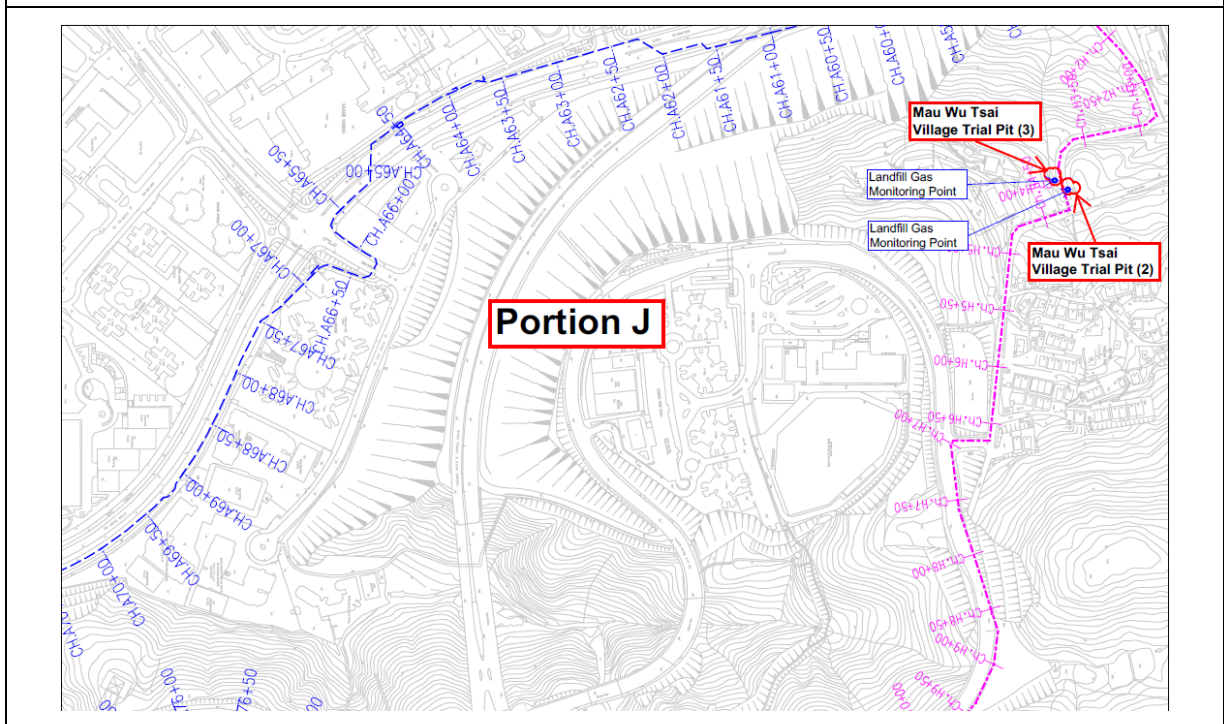


Figure 4.6c Monitoring Location – Mau Wu Tsai 3

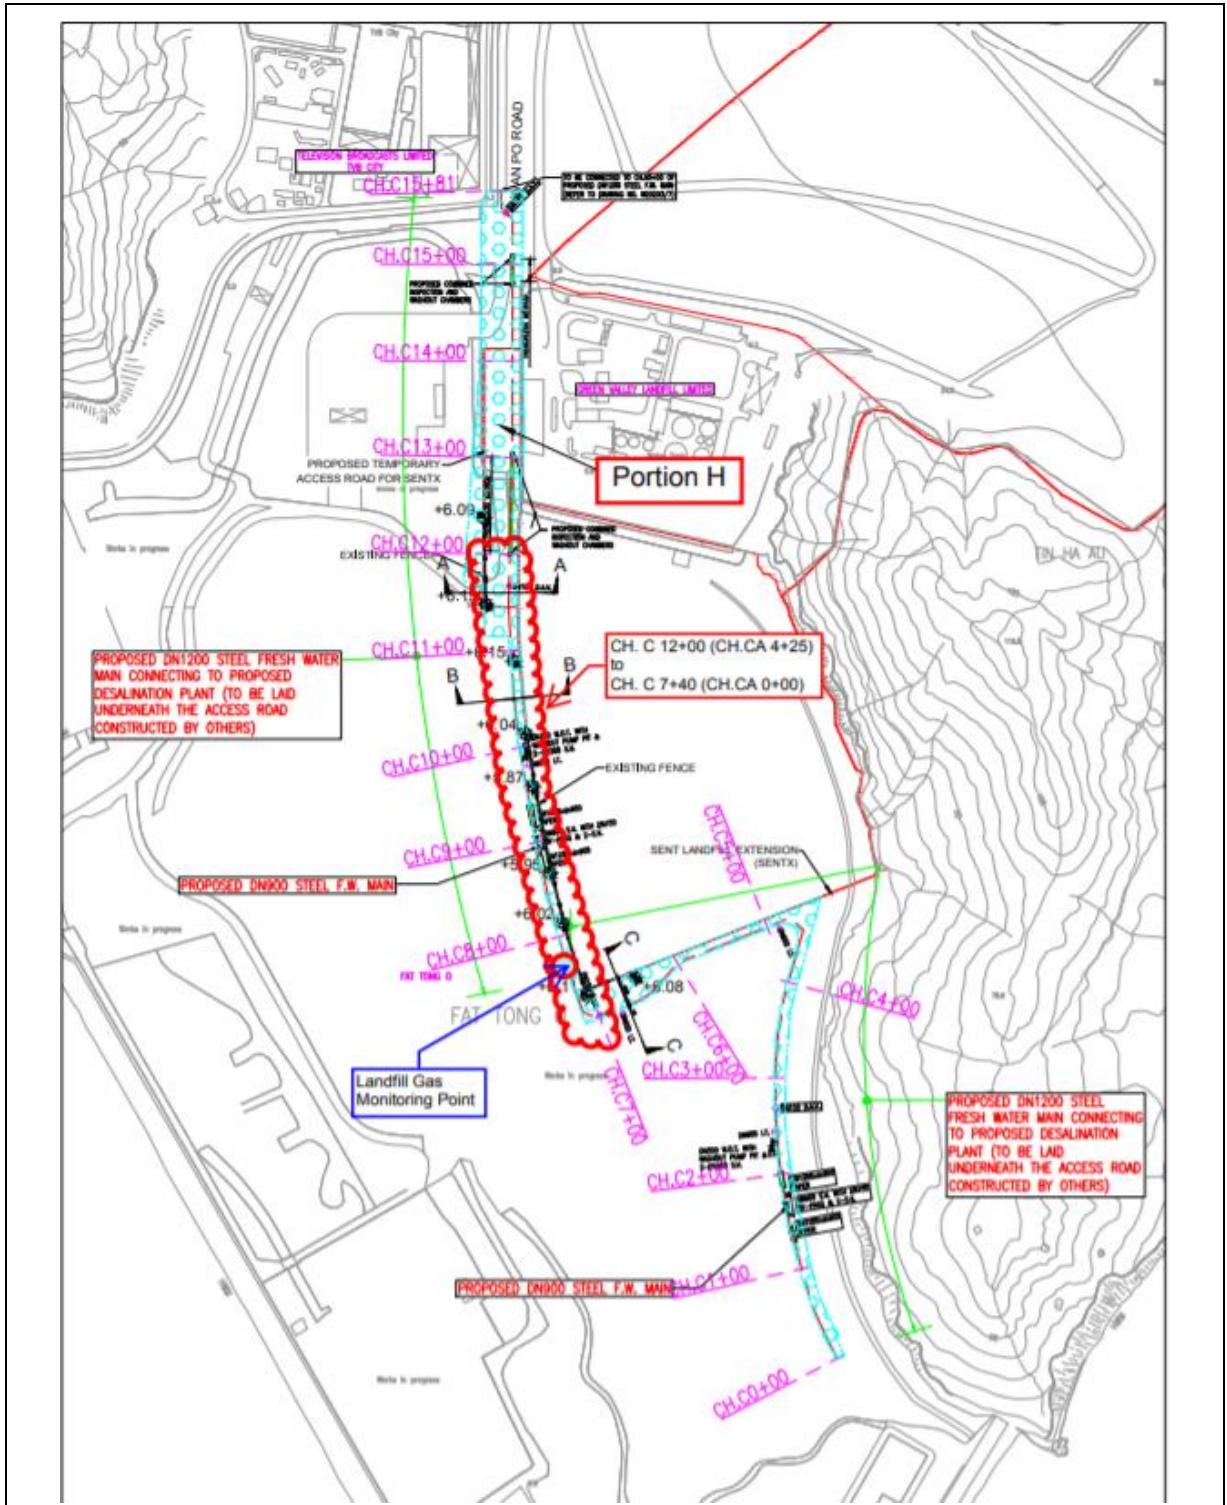


Figure 4.7 Monitoring Location –CH.CA 0+00 to CH.CA 04+25 (CH.C 7+40 ~ 12+00)



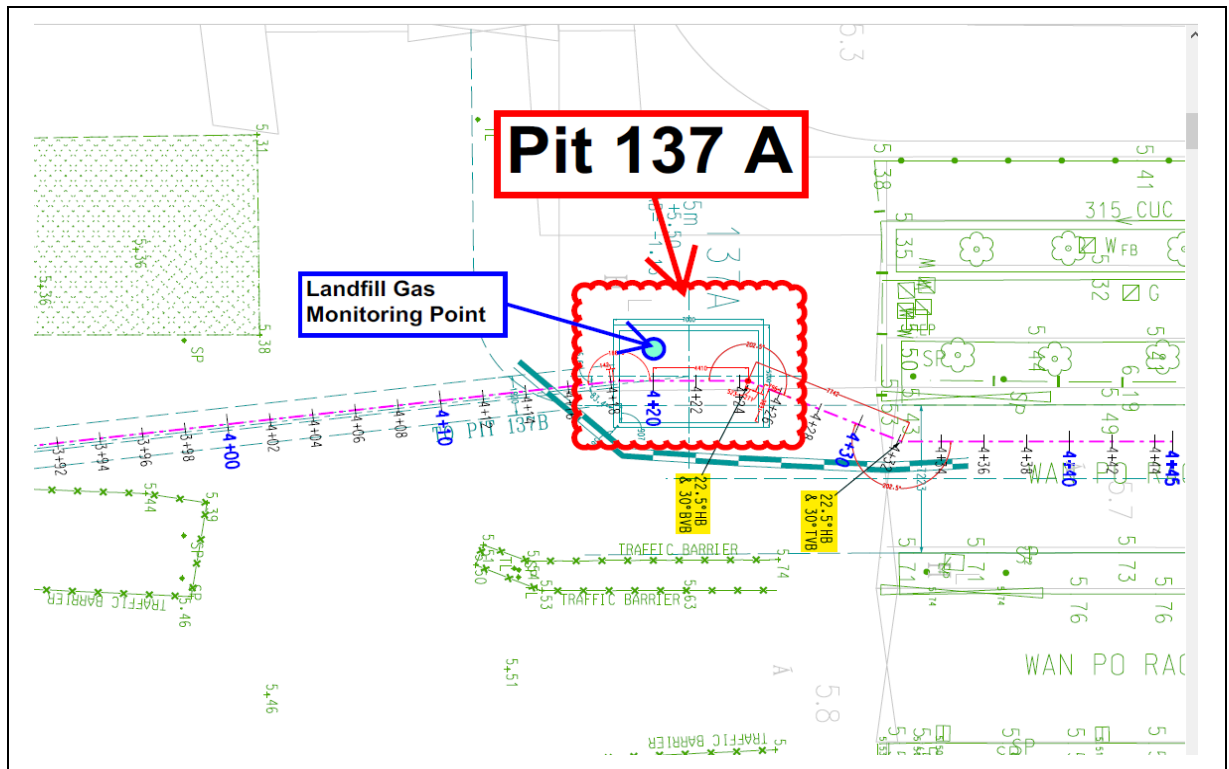


Figure 4.8a Monitoring Location – Pit 137A (137 Pit A)



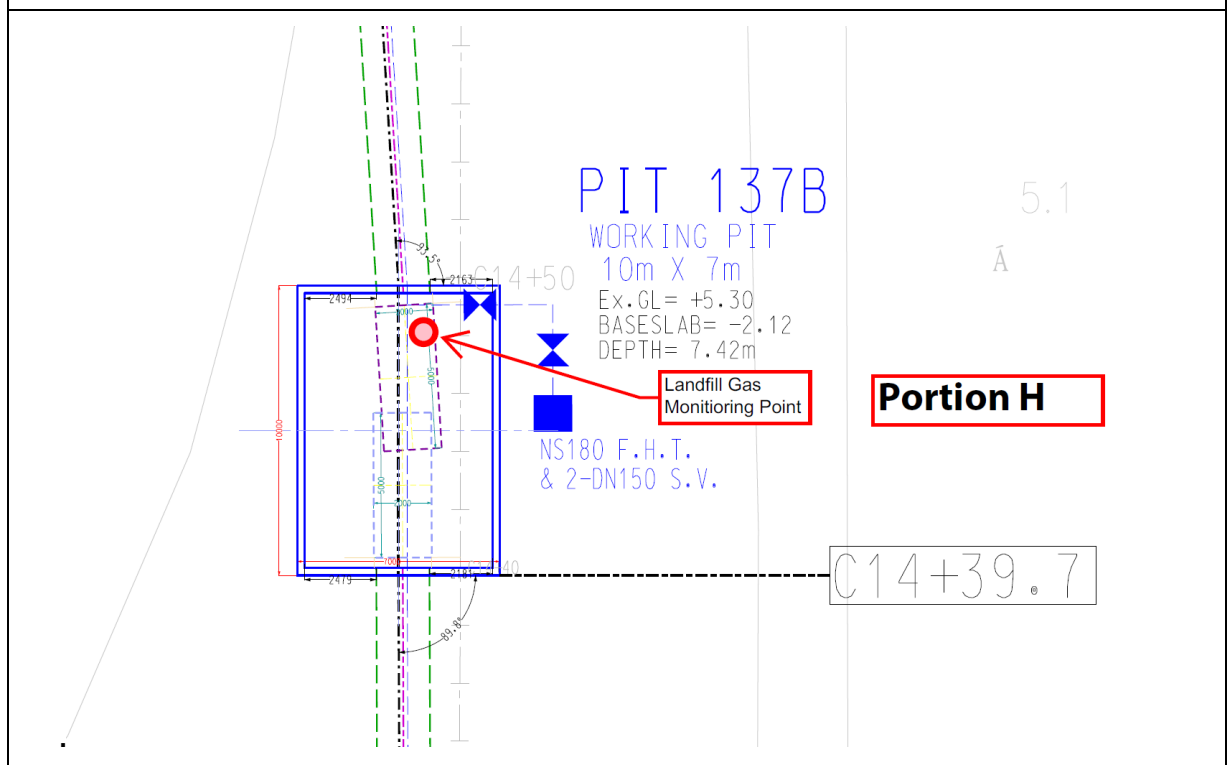


Figure 4.8b Monitoring Location – Pit 137B (137 Pit B)

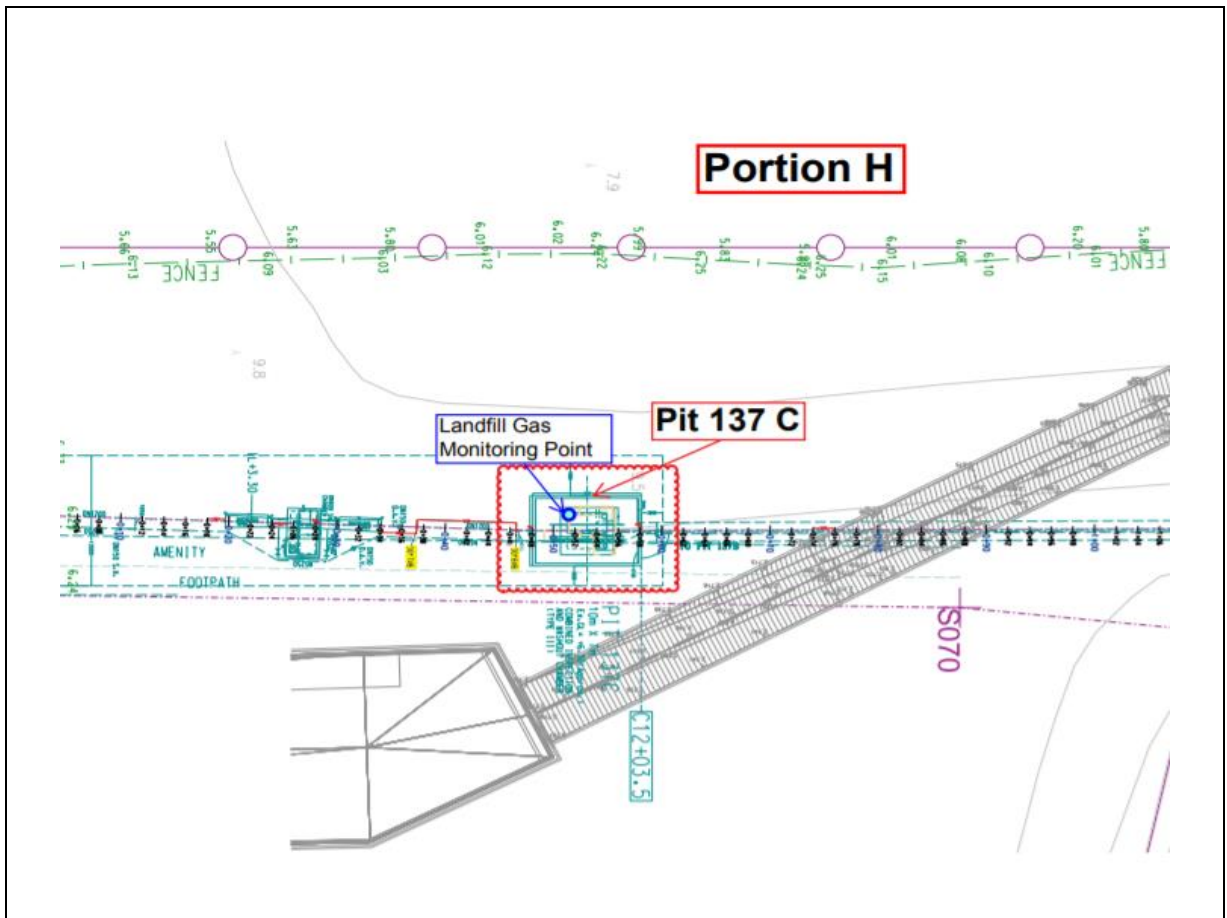

**Figure 4.8c Monitoring Location – Pit 137C (137 Pit C)**

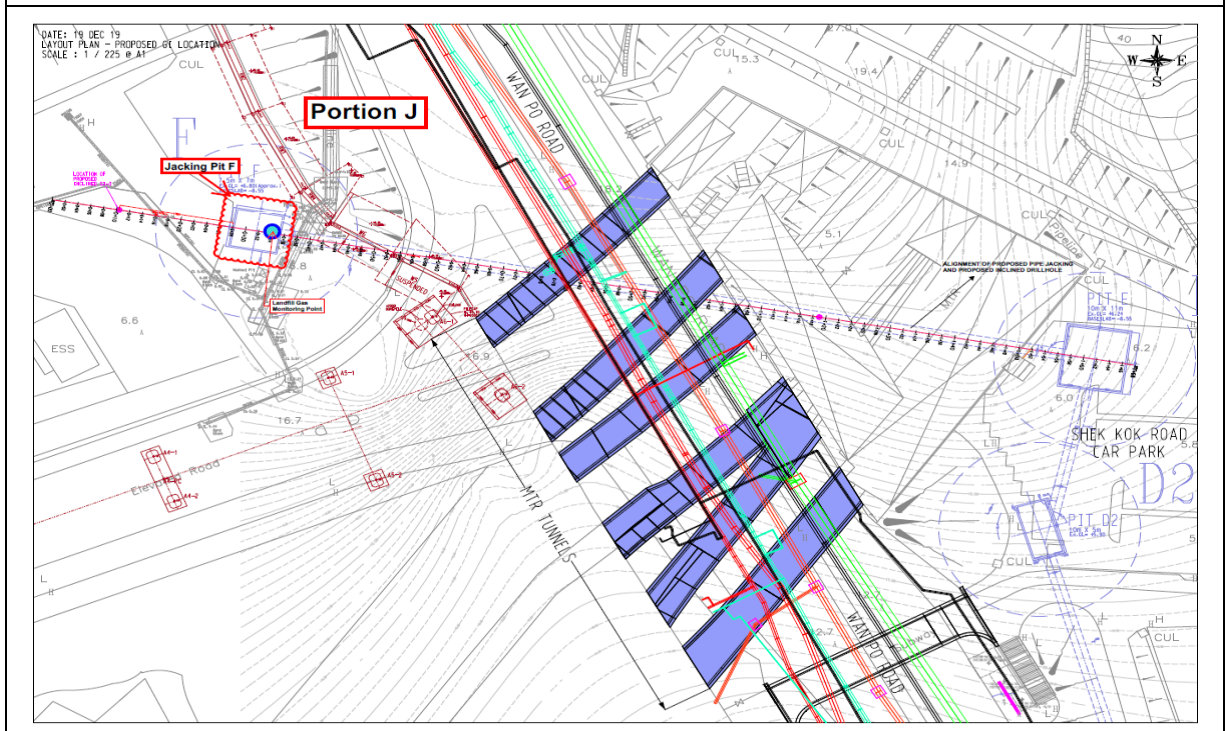

**Figure 4.9 Monitoring Location – Jacking Pit F**

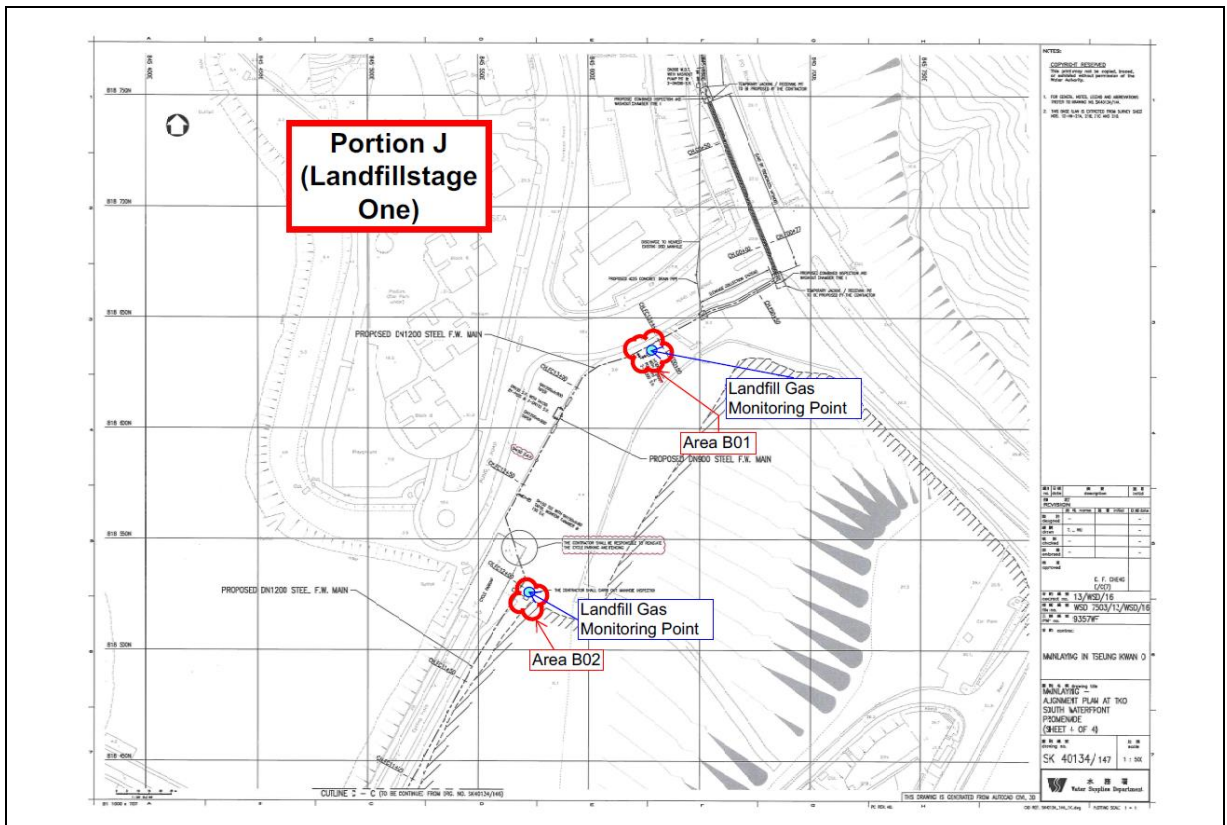


Figure 4.10a Monitoring Location – Landfill Stage 1 (Area B01-B02)

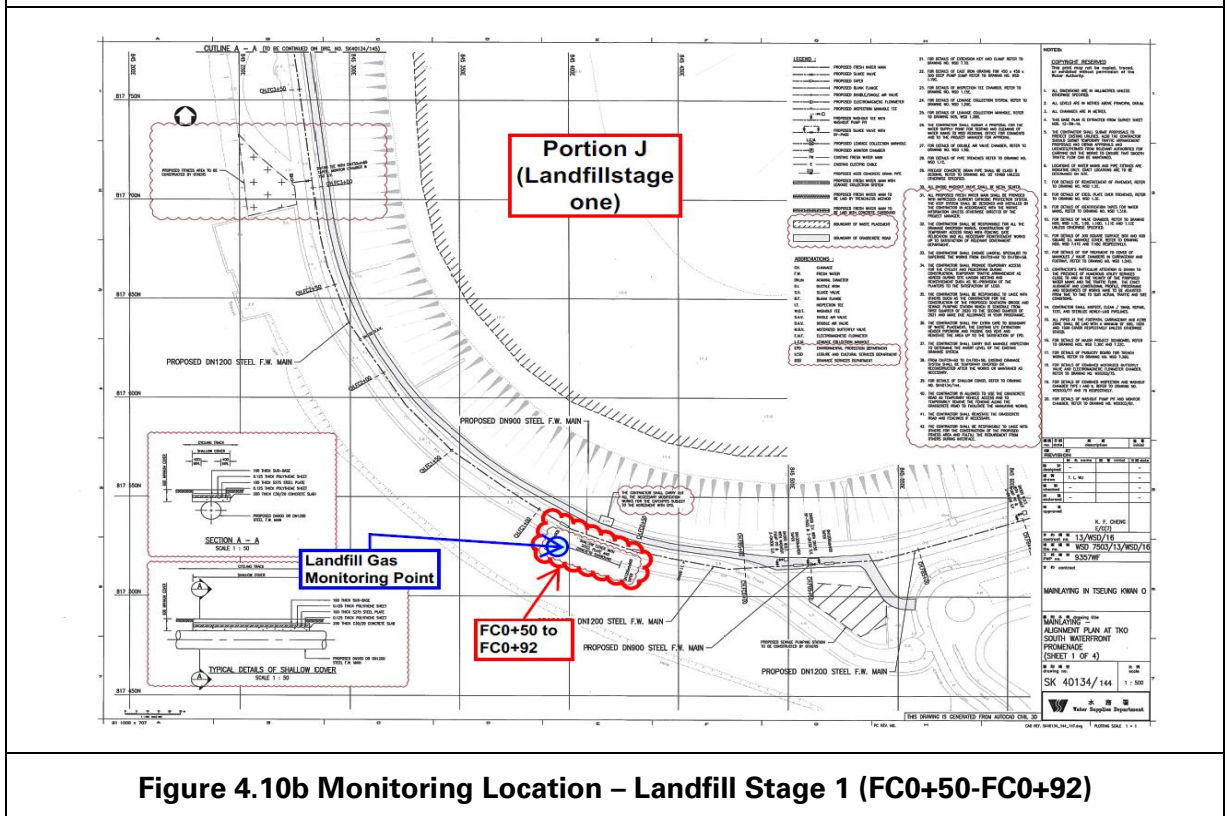


Figure 4.10b Monitoring Location – Landfill Stage 1 (FC0+50-FC0+92)

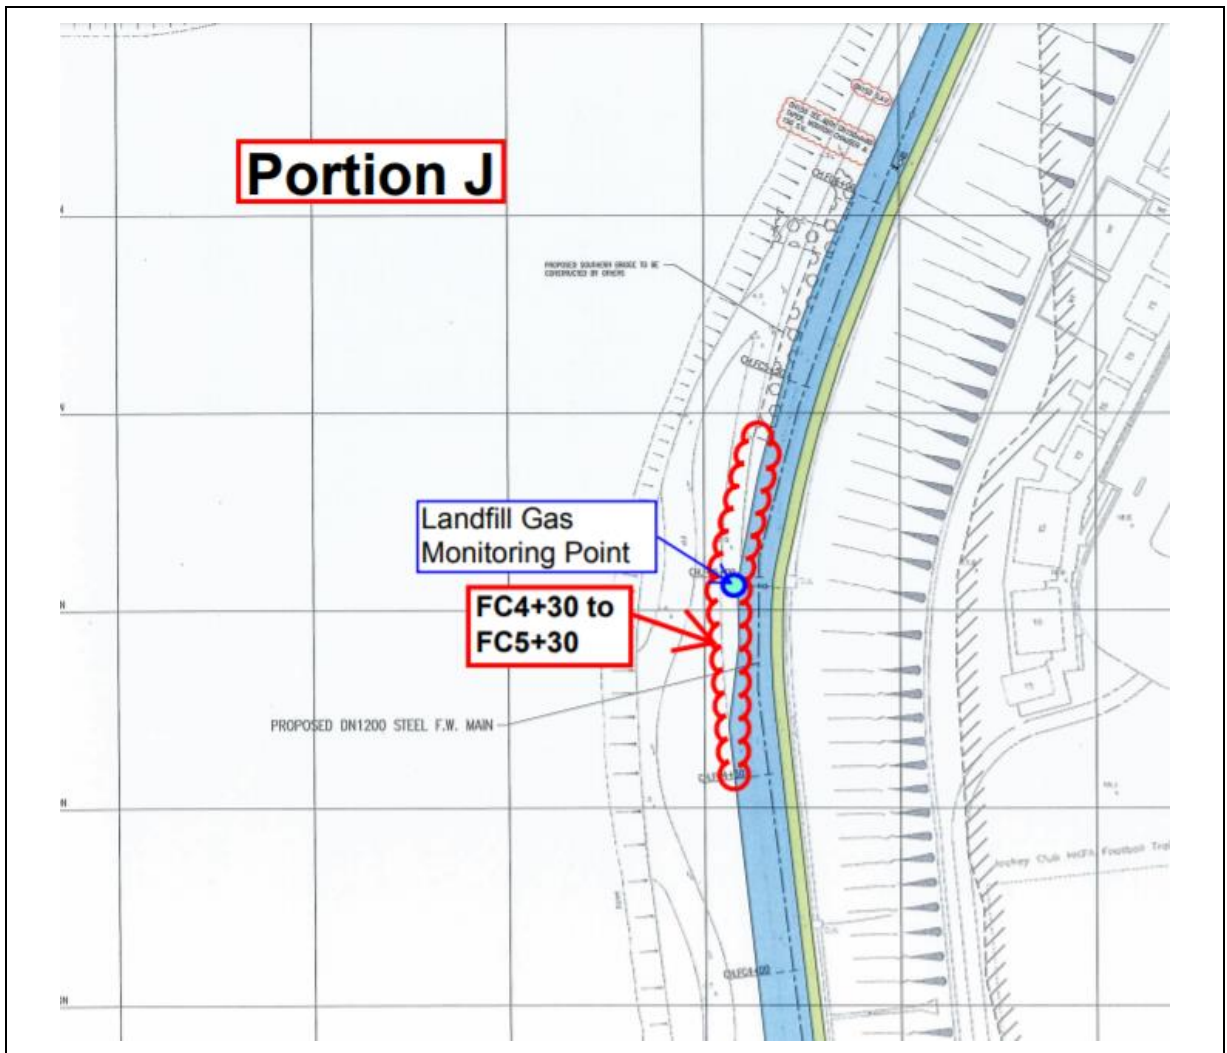


Figure 4.10c Monitoring Location – Landfill Stage 1 (FC4+30-FC5+30)

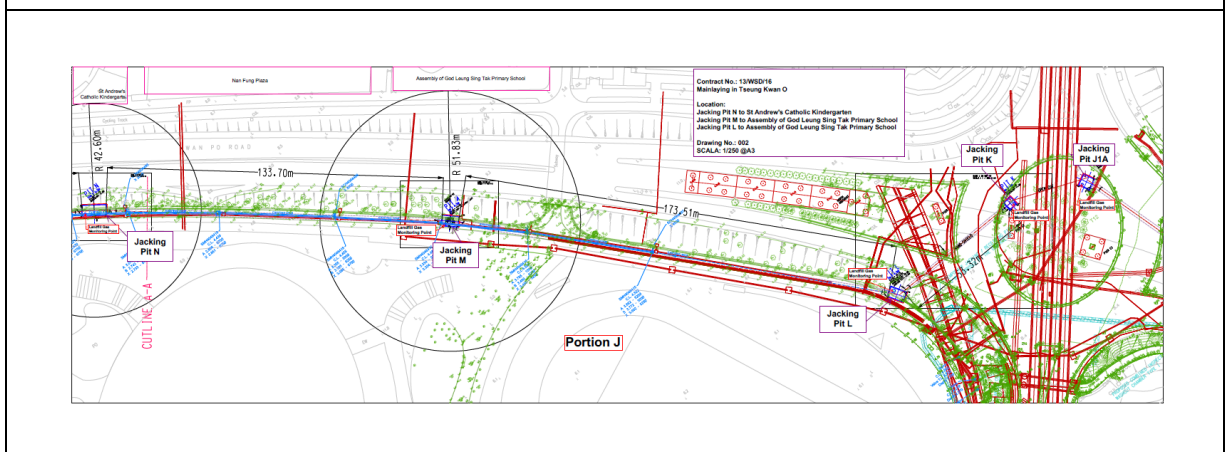


Figure 4.11a Monitoring Location – Pit L-M-N, J1A, K

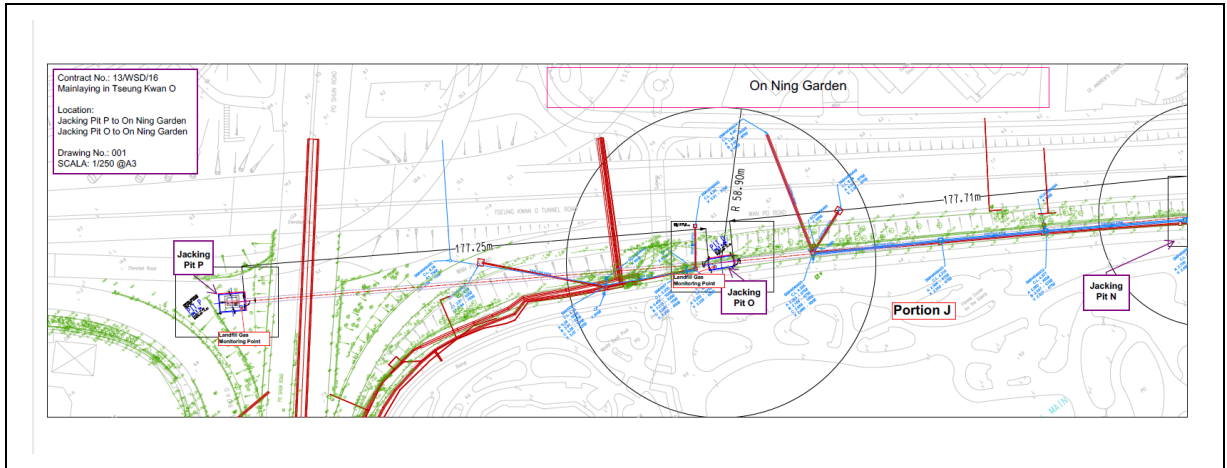


Figure 4.11b Monitoring Location – Pit N-O-P

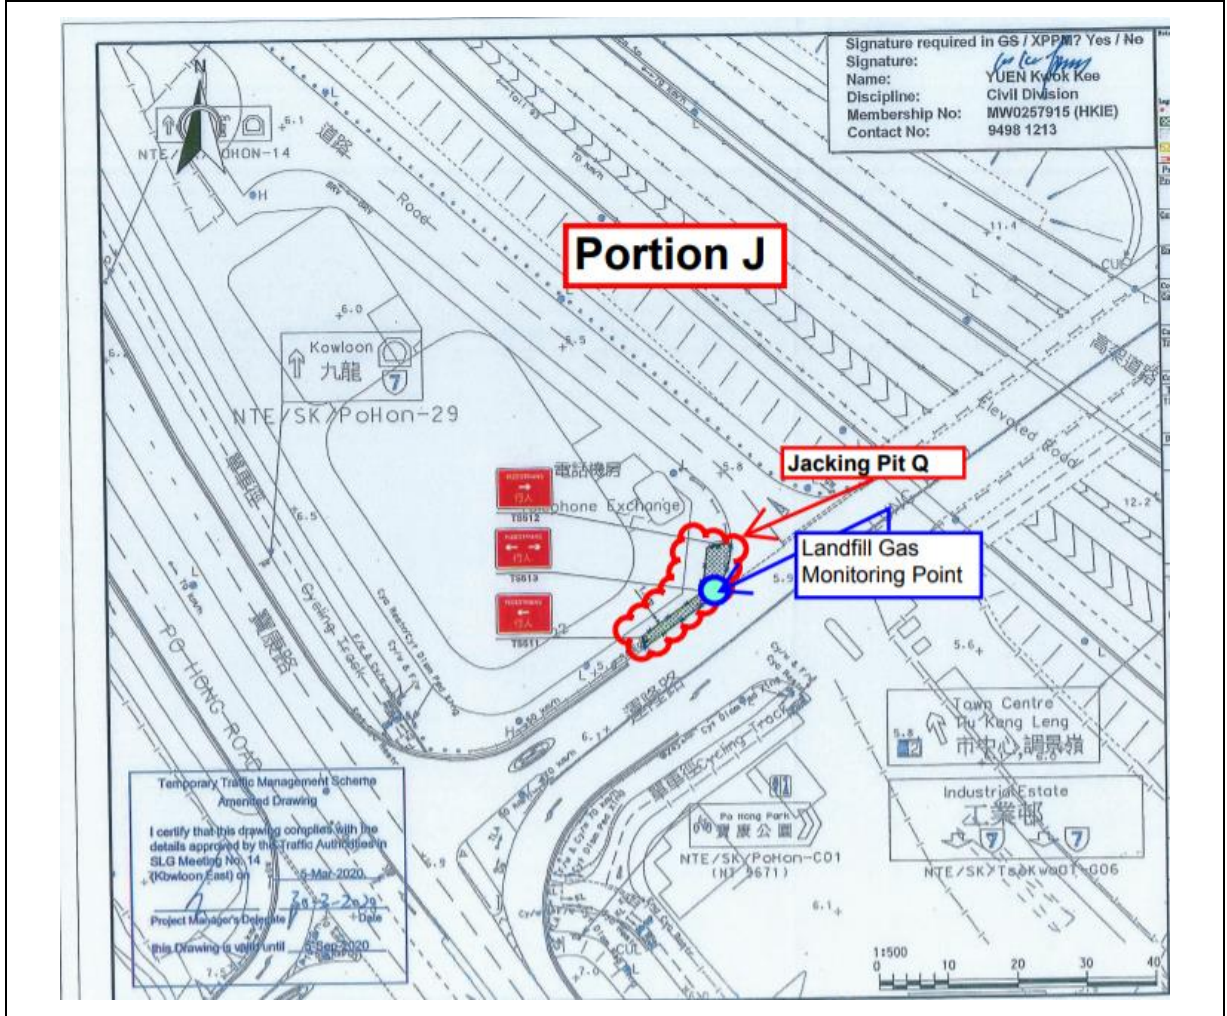


Figure 4.11c Monitoring Location – Pit Q

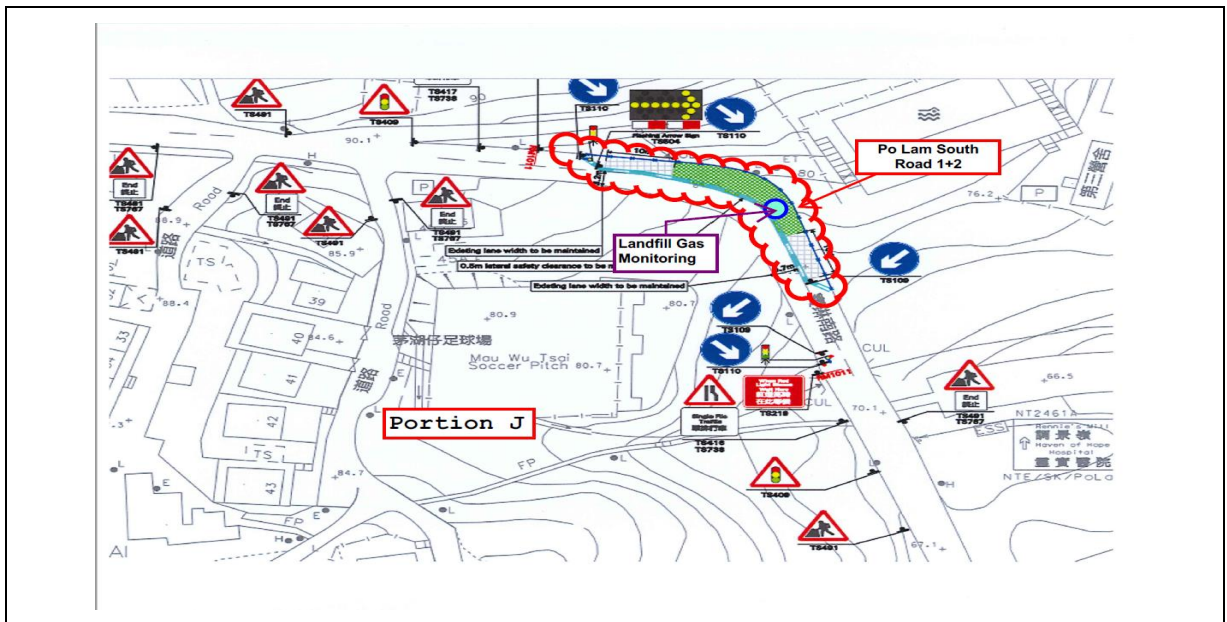


Figure 4.12 Po Lam South Road




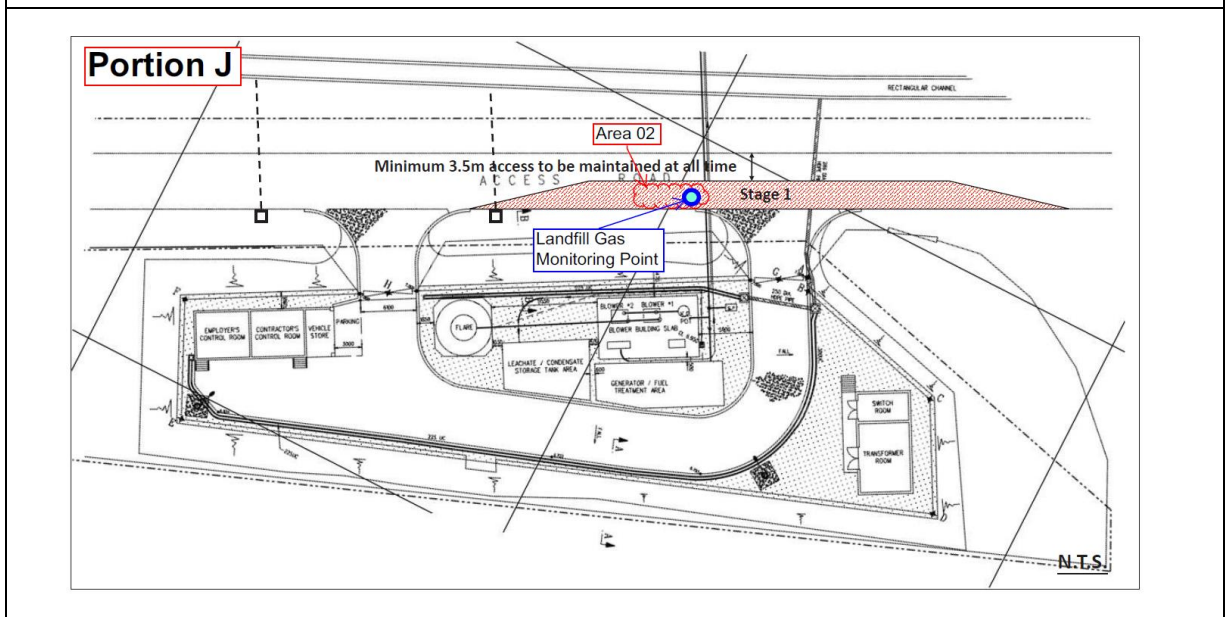


Figure 4.13 Monitoring Location – Area A02

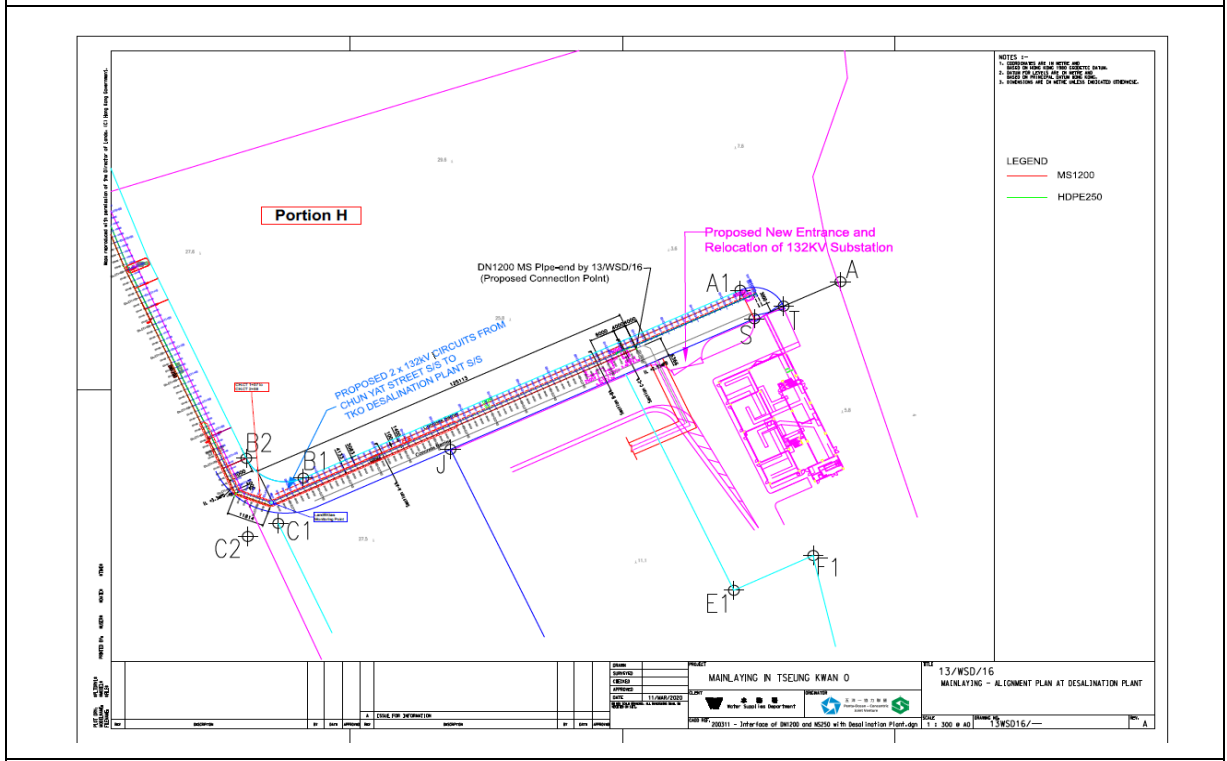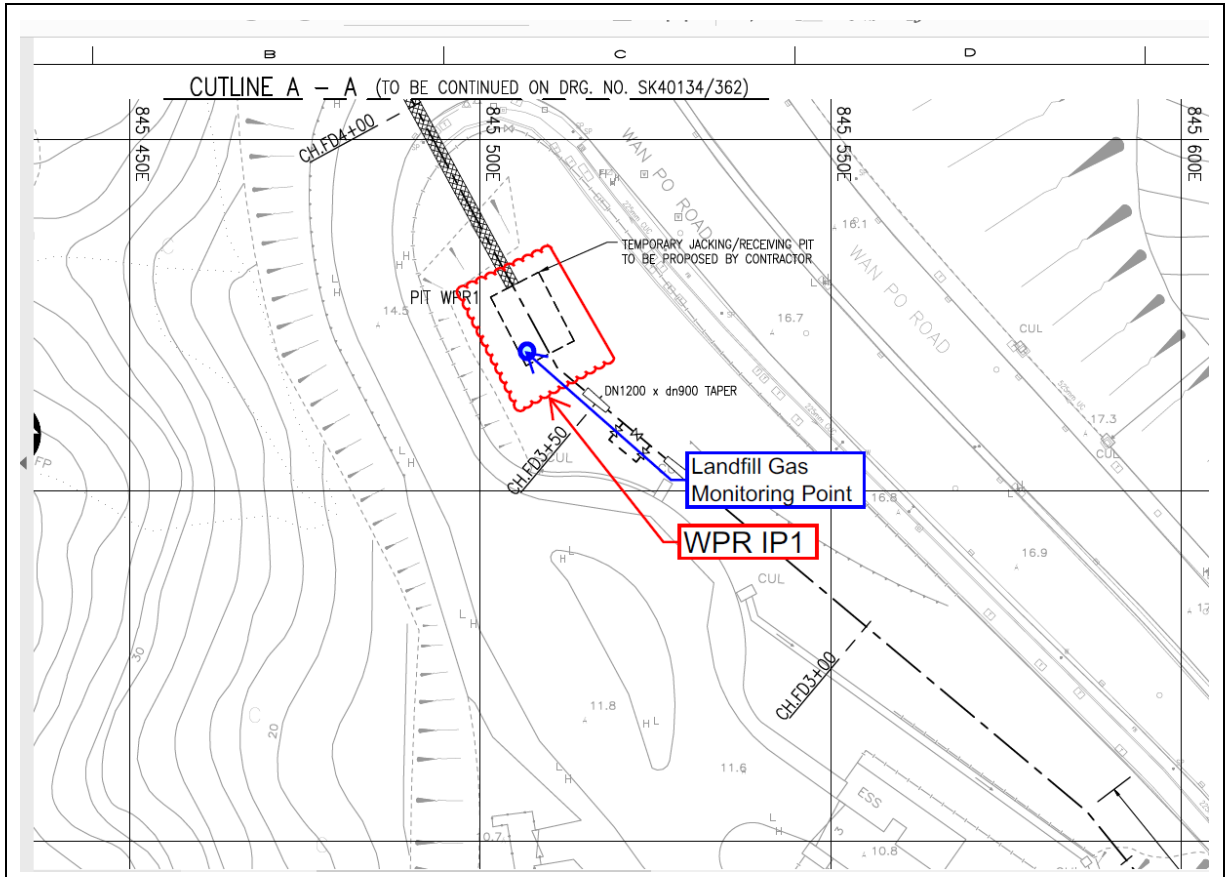

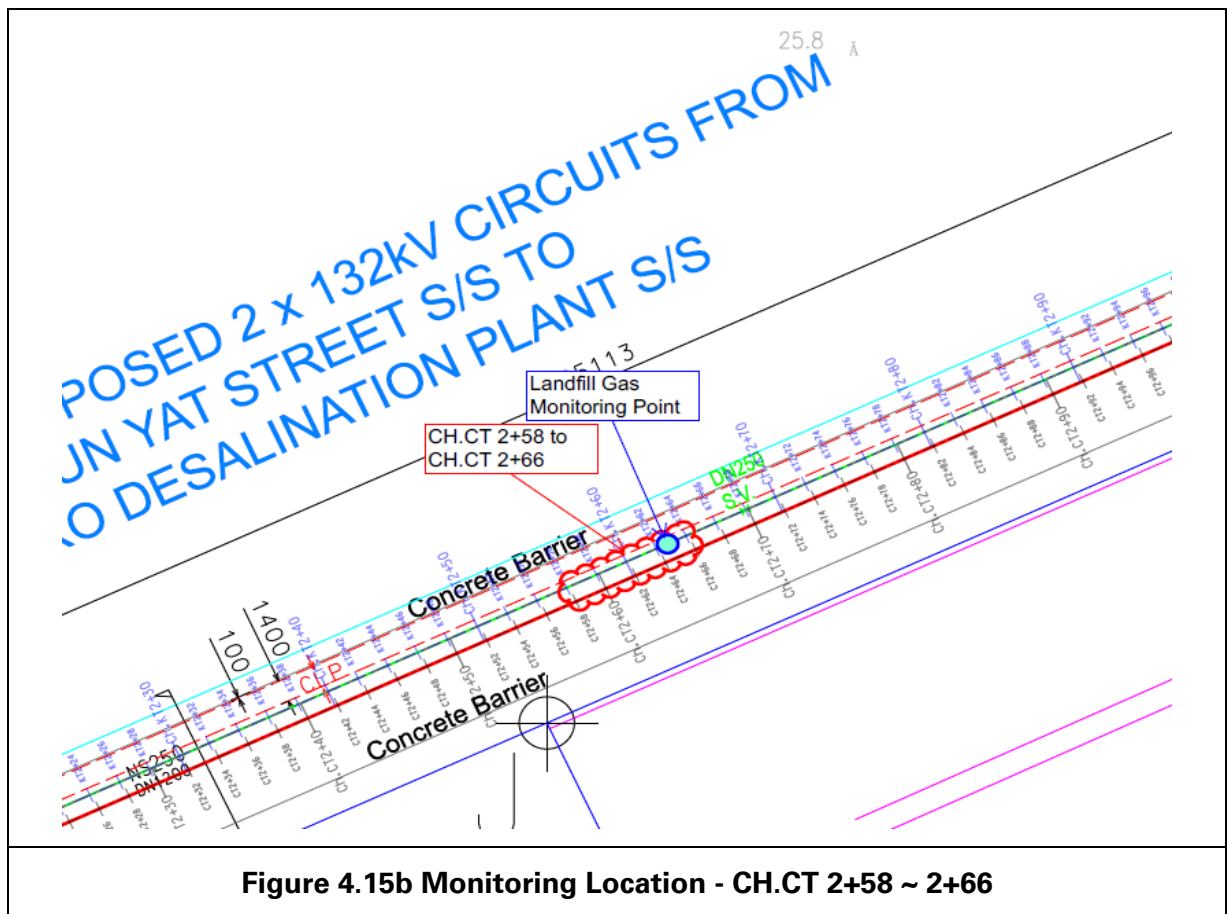

#### 4.3 Monitoring Parameters

LFG monitoring was carried out to identify any migration between the landfill and the Project and to ensure the safety of the construction, operation and maintenance personnel working on-site, visitors and any other person within the Project area.

The following parameters were monitored:

- Methane.
- Oxygen.
- Carbon Dioxide.
- Barometric Pressure.

#### 4.4 Action and Limit Level

Action and Limit Level are provided in **Table 4.1**.



Table 4.1 Action and Limit Level for Landfill Gas Monitoring Equipment

Parameters	Action Level	Limit Level
Oxygen (O <sub>2</sub> )	<19% O <sub>2</sub>	<19% O <sub>2</sub>
Methane (CH <sub>4</sub> )	>10% LEL	>80% LEL
Carbon Dioxide (CO <sub>2</sub> )	>0.5% CO <sub>2</sub>	>1.5% CO <sub>2</sub>

#### 4.5 Monitoring Equipment

Landfill Gas monitoring was carried out using intrinsically-safe, portable multi-gas monitoring instruments. The gas monitoring equipment is:

- Comply with the Landfill Gas Hazard Assessment Guidance Note as intrinsically safe;
- Capable of continuous barometric pressure and gas pressure measurements;
- Normally operate in diffusion mode unless required for spot sampling, when it should be capable of operating by means of an aspirator or pump;
- Have low battery, fault and over range indication incorporated;
- Store monitoring data, and shall be capable of being down-loaded directly;
- Measure in the following ranges:

methane	0-100% Lower Explosion Limit (LEL) and 0 100% v/v;
oxygen	0-25% v/v;
carbon dioxide	0-100% v/v; and
barometric pressure	mBar (absolute)

- alarm (both audibly and visually) in the event that the concentrations of the following are exceeded:

methane	>10% LEL;
oxygen	<19% by volume; and
carbon dioxide	>0.5% by volume
barometric pressure	mBar (absolute)

Monitoring Equipment used in the reporting period are summarised in **Table 4.2**. The Landfill Gas monitoring equipment calibration certificate is presented in **Appendix I**.

**Table 4.2 Landfill Gas Monitoring Equipment**


Equipment	Brand and Model	Calibration Expiry Date
Portable Gas Detector	QRAE III	27 July 2021

#### 4.6 Monitoring Results

In the reporting period, construction works within the consultation zones, excavations of 1m depth or more was monitored. Landfill gas monitoring was carried out by the Registered Safety Officer by the Contractor at the excavation locations for 698 times. All the measured results were presented in **Appendix J** and within the Action and Limit Levels.

## 5. SUMMARY OF MONITORING EXCEEDANCE, COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS

5.1 The Environmental Complaint Handling Procedure is shown in below **Figure 5.1:**

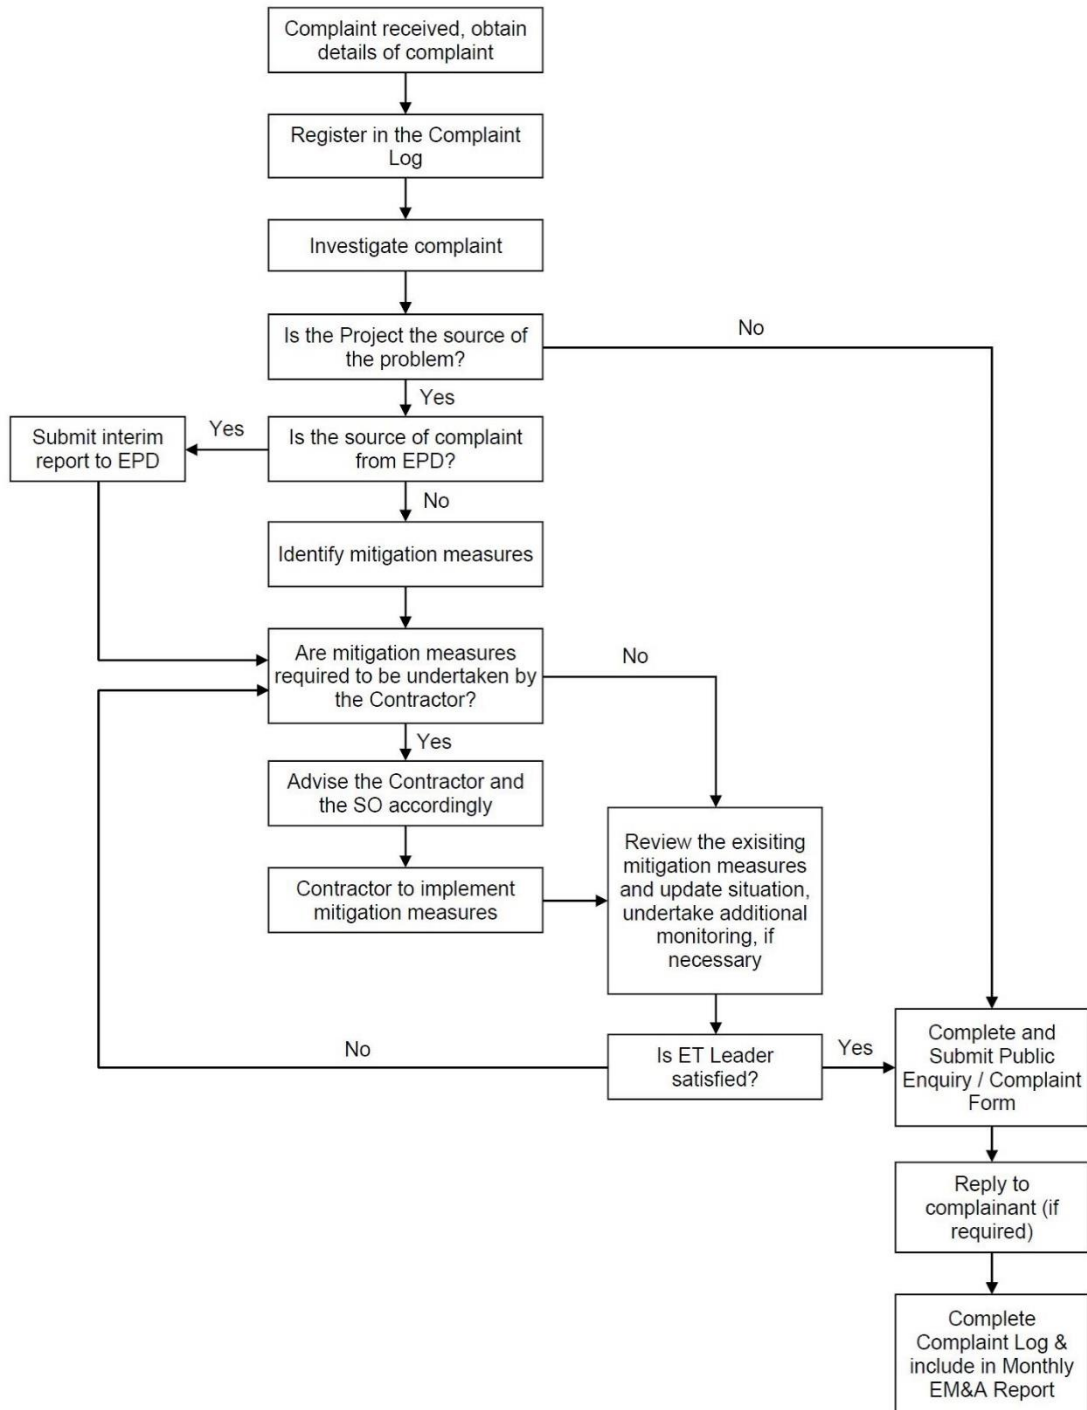

**Figure 5.1 Environmental Complaint Handling Procedure**

- 5.2 Impact monitoring for noise impact was conducted in the reporting month for NSR4 – Creative Secondary School on 8, 13, 21 and 27 January 2021 as construction works were conducted within 300m to the noise sensitive receiver. Detailed monitoring results can be found in **Appendix G**.
- 5.3 The Education Bureau (EDB) has announced that all kindergartens as well as primary and secondary schools (including special schools and schools offering non-local curriculum) will continue to suspend face to face classes and school activities until the beginning of school’s Chinese New Year holiday due to the spread of the Novel Coronavirus. Hence the noise limit level will be 70.0 dB(A). Further information and Academic School Calendar can be found in Appendix O.
- 5.4 No project-related exceedance of the Action Level was recorded during the reporting period.
- 5.5 No project-related complaints that will affect compliances to EM&A manual and environmental permit was received in the reporting month.
- 5.6 No notification of summons and prosecution was received in the reporting period.
- 5.7 Statistics on complaints and regulatory compliance are summarized in **Appendix K**.

## 6. EM&A SITE INSPECTION

- 6.1 Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, site inspections were carried out on 6, 15, 21 and 25 January at the site portions list in **Table 6.1** below.

**Table 6.1 Site Inspection Record**

Date	Inspected Site Portion	Time
06 January 2021	Portion J	9:30am – 11:30am
15 January 2021	Portion J	14:20pm – 17:00pm
21 January 2021	Portion J and H	9:30am – 11:30am
25 January 2021	Portion J	9:30am – 12:00pm

- 6.2 One joint site inspection with IEC was carried out on 25 January 2021.
- 6.3 Minor deficiencies were observed during weekly site inspection. Key observations during the site inspections are summarized in **Table 6.2**.

**Table 6.2 Site Observations**

Date	Environmental Observations	Follow-up Status
06 January 2021	<ol style="list-style-type: none"> <li>1. Gully was not properly covered with geo-textile and sandbags at four sides at Pit D and CHA5+90.</li> <li>2. Chemical spillage was found at CHA5+90.</li> <li>3. Environmental permit was not observed at the vehicle exit/entrance at CHA5+90.</li> <li>4. Construction boundaries was not enclosed fully at Pit B.</li> </ol>	<ol style="list-style-type: none"> <li>1. The materials were cleaned near the gully or gullies were covered with geo-textile.</li> <li>2. Chemical spillage was cleaned.</li> <li>3. Environmental permit was added.</li> <li>4. Construction boundaries were enclosed fully.</li> </ol>
15 January 2021	<ol style="list-style-type: none"> <li>1. Environmental permit was not observed at the site entrance/exit at Wan Po Road 1, Wan Po Road 2, CH.FC 3+62.</li> <li>2. Gullies were not properly protected by sandbags and geotextile at Wan Po Road 3, CH.FC 3+62 and CH.FC 7+42.</li> </ol>	<ol style="list-style-type: none"> <li>1. Environmental permit was added.</li> <li>2. Gullies were properly protected by geotextile.</li> </ol>
21 January 2021	<ol style="list-style-type: none"> <li>1. Construction boundaries were not fully protected by sandbags at Wan Po Road 1.</li> <li>2. Environmental permit was not observed at the site entrance/exit at 137 Pit C.</li> <li>3. Gully was not protected by sandbags and geo-textile at Wan Po Road 1.</li> <li>4. Chemicals were not placed inside a drip tray at Wan Po Road 1.</li> </ol>	<ol style="list-style-type: none"> <li>1. Construction boundaries were fully protected.</li> <li>2. Environmental permit was observed.</li> <li>3. Gully was protected by timber block and geo-textile. Using Timber block for avoiding sand bag damage by excavator.</li> <li>4. Chemicals were removed.</li> </ol>
25 January 2021	<ol style="list-style-type: none"> <li>1. The desilting or water treatment facility was observed leaking. The contractor was reminded to replace a new water treatment facility to ensure proper treatment of wastewater before</li> </ol>	<ol style="list-style-type: none"> <li>1. The desilting or water treatment facility was changed a new one.</li> <li>2. Grab was removed.</li> </ol>

Date	Environmental Observations	Follow-up Status
	discharge at Hong Kong Velodrome. 2. Grab was not placed on top of a tarpaulin sheet which may lead to accidental contamination of the ground by chemical at Hong Kong Velodrome.	

6.4 According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents should be implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix C**.

6.5 Site inspection proforma of the reporting period is provided in **Appendix L**.

## 7. FUTURE KEY ISSUES

7.1 Key works that will be anticipated in the next reporting period for the Project are shown in **Table 7.1**.

**Table 7.1. Key works for the next reporting month**

Location	Location	Forecast Works for January 2021
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> <li>Hydrostatic pressure testing for completed MS1200 pipeline section will be conducted.</li> </ul>
	TKO 137 Pit B	<ul style="list-style-type: none"> <li>Pipe jacking works will be commenced.</li> </ul>
	TKO 137 Pit C	<ul style="list-style-type: none"> <li>Pit excavation and ELS works will be continued.</li> </ul>
Portion J of the Project Site	Wan Po Rd – Workfront 1	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying will be conducted.</li> </ul>
	Wan Po Rd – Workfront 2	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying works will be conducted.</li> <li>Trial pit works for Pit 1 will be commenced.</li> </ul>
	Wan Po Rd – Workfront 3	<ul style="list-style-type: none"> <li>Trench excavation and mainlaying works will be conducted.</li> </ul>
	Wan Po Rd – Pit A	<ul style="list-style-type: none"> <li>Excavation and ELS works will be conducted.</li> </ul>
	Wan Po Rd – Pit B	<ul style="list-style-type: none"> <li>Excavation and ELS works will be conducted.</li> </ul>
	Landfill Stage 1 – Area A	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying works will be conducted.</li> </ul>
	Landfill Stage 1 – Area B	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying works will be conducted.</li> </ul>
	Cycle Track – Workfront 1	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying works will be conducted.</li> </ul>
	Cycle Track – Workfront 2	<ul style="list-style-type: none"> <li>Trench excavation and pipe laying works will be conducted.</li> </ul>
	Velodrome – Pit K	<ul style="list-style-type: none"> <li>Trenchless pit for hand-shield works will be conducted</li> </ul>
	Velodrome – Pit L	<ul style="list-style-type: none"> <li>Trenchless pit for hand-shield works will be conducted</li> </ul>
	Velodrome – Pit M	<ul style="list-style-type: none"> <li>Pipe jacking works will be continued.</li> </ul>
	Velodrome – Pit O	<ul style="list-style-type: none"> <li>Pipe jacking works will be continued.</li> </ul>
	Mau Wu Tsai – Workfront 1	<ul style="list-style-type: none"> <li>Trench excavation and pipe mainlaying works will be conducted.</li> </ul>
	Mau Wu Tsai – Workfront 2	<ul style="list-style-type: none"> <li>Trench excavation and pipe mainlaying works will be conducted</li> </ul>

7.2 The major environmental impacts brought by the above construction works will include:

- Construction dust and noise generation of saw cutting of concrete surface, mainlaying of pipes, pipe piling, excavation works and ELS works.
  - Waste generation from construction activities
- 7.3 The key environmental mitigation measures for the Project in the coming reporting period associated with the above construction works will include:
- Dust suppression by regular wetting and water spraying for saw cutting of concrete surface, mainlaying of pipes, pipe piling, excavation works and ELS works
  - Reduction of noise from equipment and machinery on-site
  - Sorting and storage of general refuse and construction waste
- 7.4 The proactive environmental protection proforma for the next reporting month is listed in **Appendix M**.
- 7.5 Referring to EM&A Manual Section 4.1.2, the impact noise monitoring should be carried out at all the designated monitoring stations when there are project-related construction activities undertaken within a radius of 300m from the monitoring stations.
- 7.6 The tentative impact monitoring schedule for the next reporting month is attached in **Appendix N**.



## 8. CONCLUSION AND RECOMMENDATIONS

- 8.1 This is the 30<sup>th</sup> monthly Environmental Monitoring and Audit (EM&A) Report presenting the EM&A works undertaken during the period from 1 January 2021 to 31 January 2021, in accordance with the EM&A Manual and the requirement under EP-503/2015/A.
- 8.2 Impact monitoring for noise impact was conducted in the reporting month for NSR4 – Creative Secondary School on 8, 13, 21 and 27 January 2021 as construction works were conducted within 300m to the noise sensitive receiver. Detailed monitoring results can be found in **Appendix G**.
- 8.3 The Education Bureau (EDB) has announced that all kindergartens as well as primary and secondary schools (including special schools and schools offering non-local curriculum) will continue to suspend face to face classes and school activities until the beginning of school's Chinese New Year Holidays due to the spread of the Novel Coronavirus. Hence the noise limit level will be 70.0 dB(A). Further information and Academic School Calendar can be found in Appendix O.
- 8.4 No project-related exceedance of the Action Level was recorded during the reporting period.
- 8.5 Weekly environmental site inspection was conducted during the reporting period. Minor deficiencies were observed during site inspection and were rectified. The environmental performance of the project was therefore considered satisfactory.
- 8.6 According to the environmental site inspections performed in the reporting month, the contractor is reminded to pay attention on maintaining site tidiness, water treatment facilities, dust suppression mitigations and proper materials storage.
- 8.7 No project-related complaints that will affect compliances to the EM&A Manual and Environmental Permit was received in the reporting period.
- 8.8 No notification of summons or prosecution was received since the commencement of the Contract.
- 8.9 The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

# Appendix A

# Construction Programme

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




13/WSD/16 - Mainlaying in Tseung Kwan O  
 Outline Construction Programme (As on 31 Aug 2018)

YEAR	LOCATION		FROM	TO	2018												2019												2020												2021											
	PJ-ID	ROAD			1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12
<b>Section A (TKO137 to Wan Po Road)</b>																																																				
Section A1 (Open-trench)	-	Wan Po Road	0	362																																																
Section A2 (Pipe-Jacking)	A	Wan Po Road	362	530																																																
Section A3 (Open-trench)	-	Wan Po Road	530	1379																																																
Section A4 (Pipe-Jacking)	B	Wan Po Road	1379	2268																																																
Section A5 (Open-trench)	-	Wan Po Road	2268	4113																																																
<b>Section B (Po Yap Road to Po Hong Road)</b>																																																				
Section B1 (Pipe-Jacking)	C	Po Yap Road	4113	4200																																																
Section B2 (Open-trench)	-	Po Yap & Po Hong Rd	4200	5500																																																
Section B3 (Pipe-Jacking)	D1 & D2	Po Hong & Ling Hong Rd	5500	5600																																																
Section B4 (Open-trench)	-	Ling Hong Road	5600	5799																																																
Section B5 (Pipe-Jacking)	E	Po Hong Road	5799	5838																																																
Section B6 (Open-trench)	-	Po Hong Road	5838	6254																																																
Section B7 (Pipe-Jacking)	F	Po Hong Road	6254	6368																																																
Section B8 (Open-trench)	-	Po Hong Road	6368	7250																																																
<b>Section C (Po Lam Road to Tsui Lam to TKOFWPSR*)</b>																																																				
Section C1 (Open-trench)	-	Po Lam Road	7250	7740																																																
Section C2 (Pipe-Jacking)	G	Tsui Lam Road	7740	7770																																																
Section C3 (Open-trench)	-	Tsui Lam Road	7770	8300																																																
Section C4 (Slope)	-	TKOFWPSR	8300	8376																																																

# Commencement of works at CHA 720 on 30 Aug 2018.  
 \*TKOFWPSR - Tseung Kwan O Fresh Water Primary Service Reservoir  
 \*\*Remaining 1581m within TKO137 with site possession from Nov 2019


## Appendix B

# Overview of Mainlaying in Tseung Kwan O

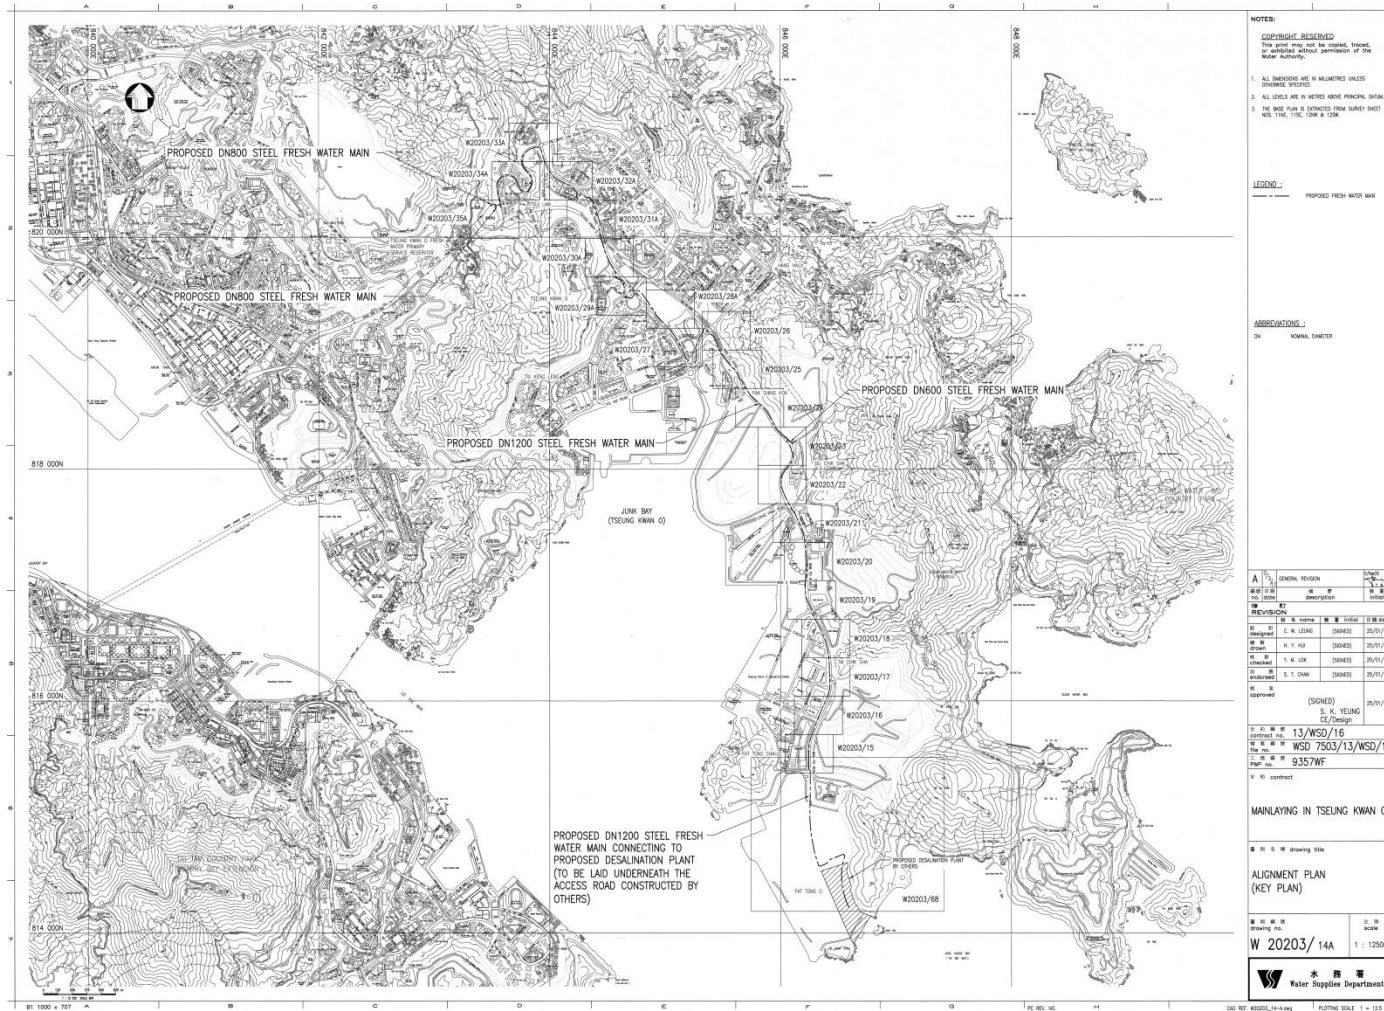

**Figure B1. Overview of Mainlaying in TKO**

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**

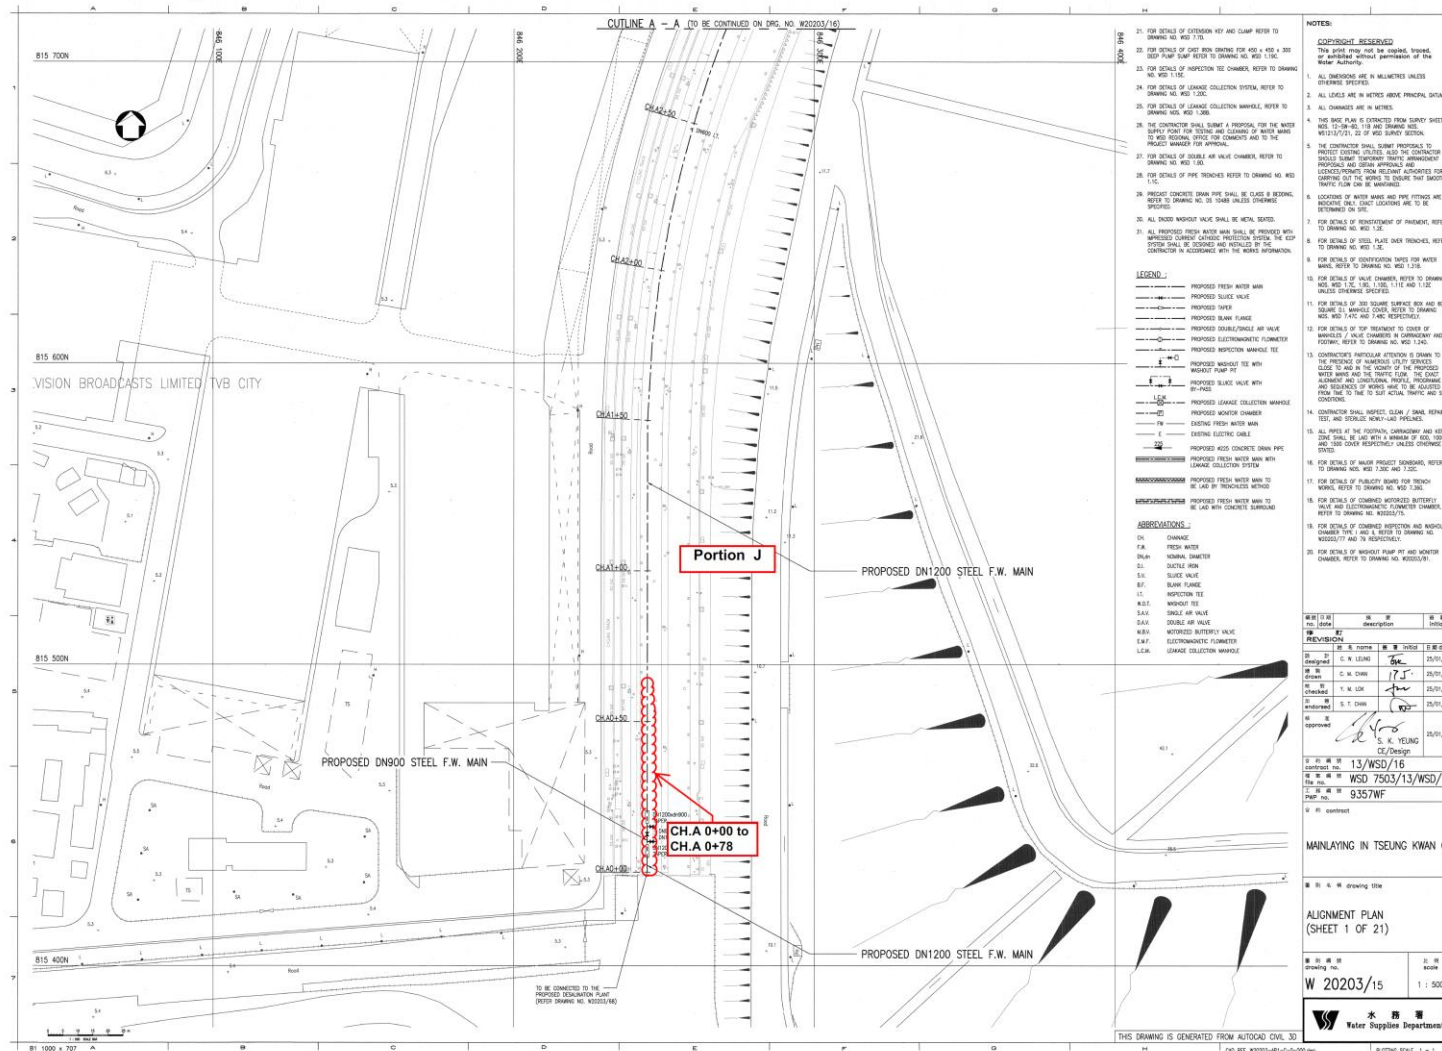

**Figure B2. Location Plan for Portion J - CH.A 0+00 to CH.A 0+78**

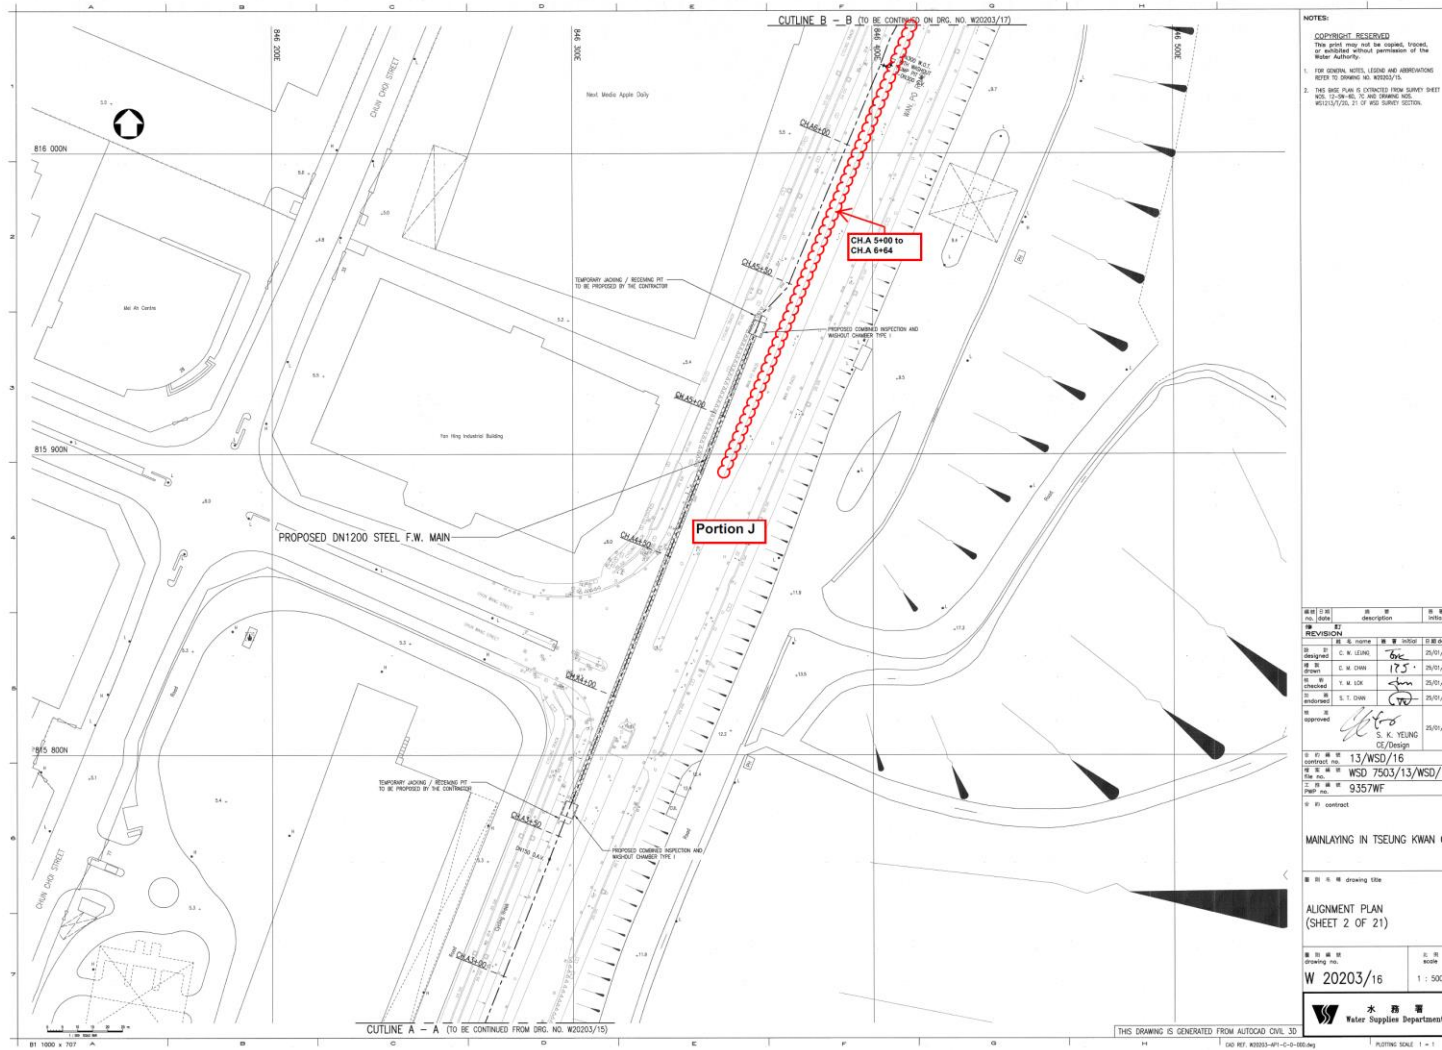
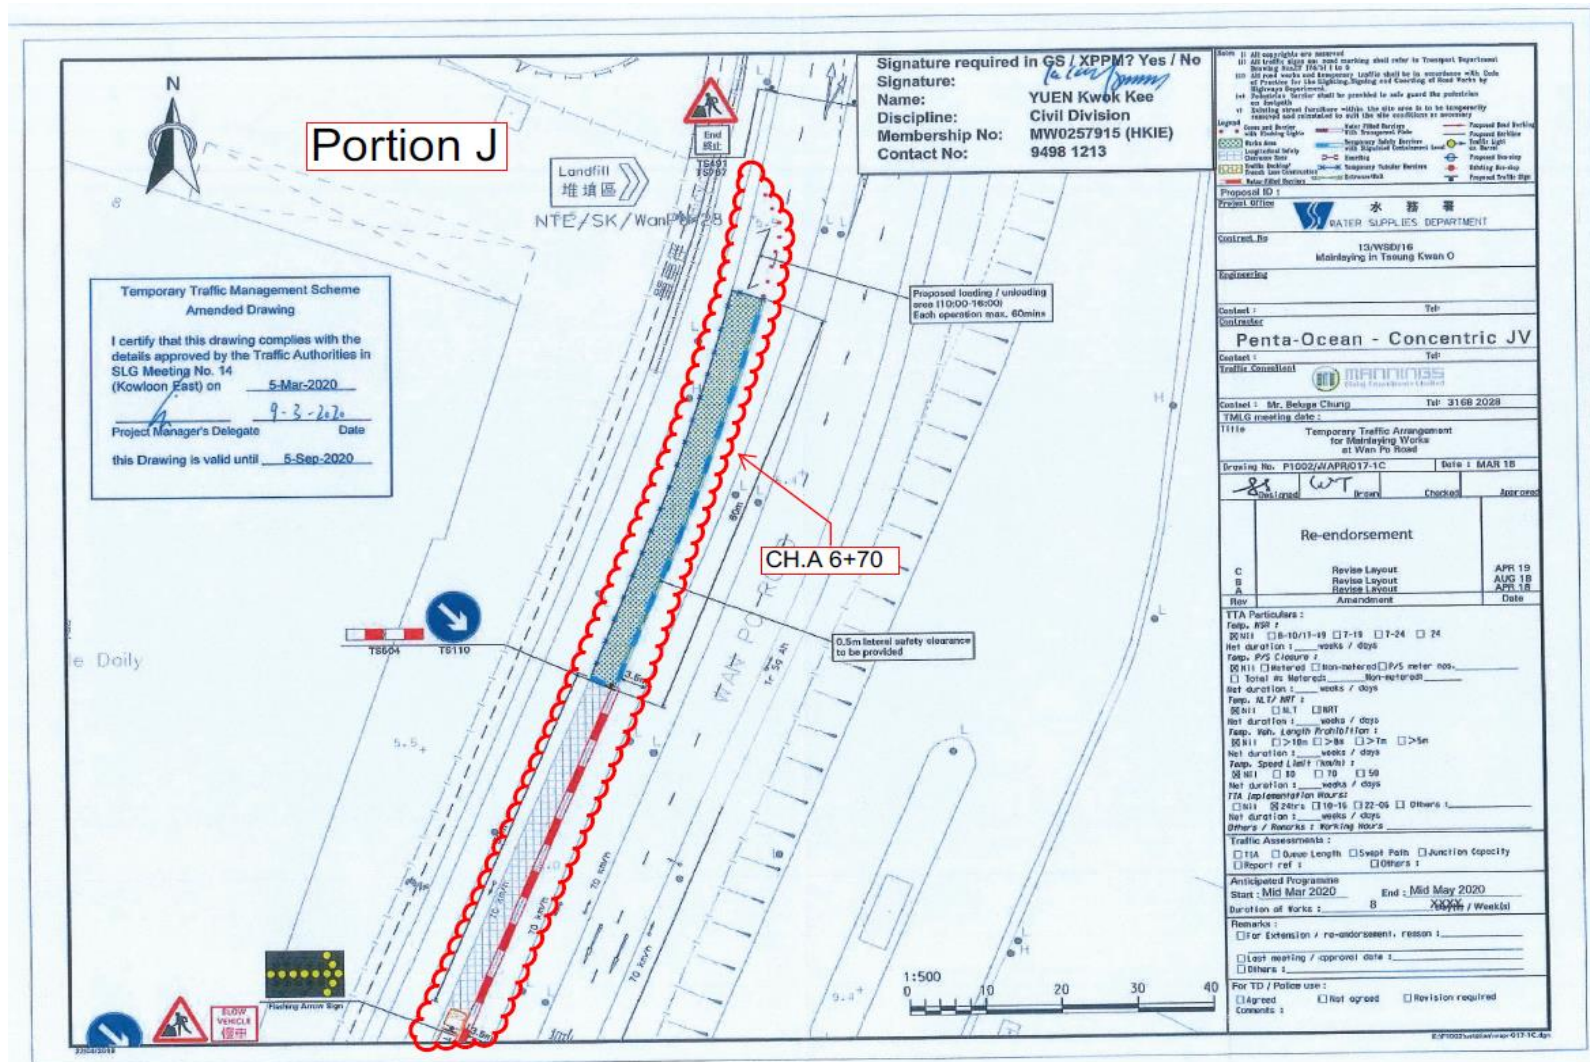


Figure B3a. Location Plan for Portion J - CH.A 5+00 to CH.A 6+64






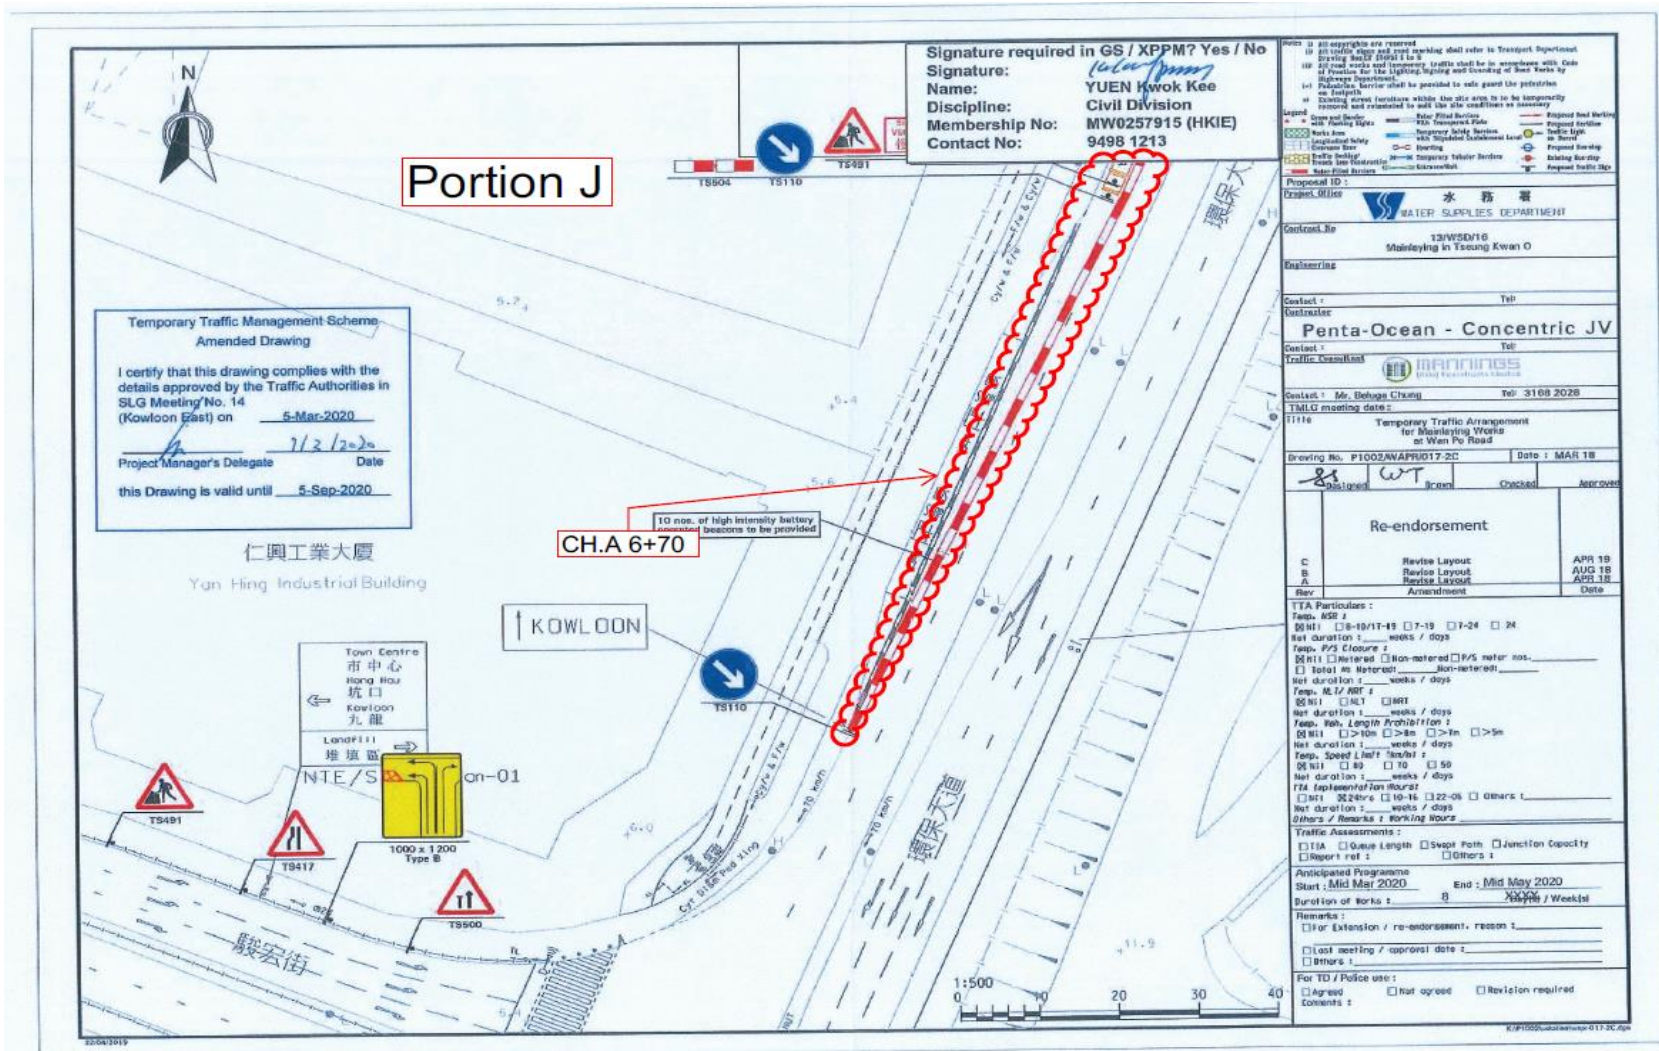


Figure B3b. Location Plan for Portion J - CH.A 6+70

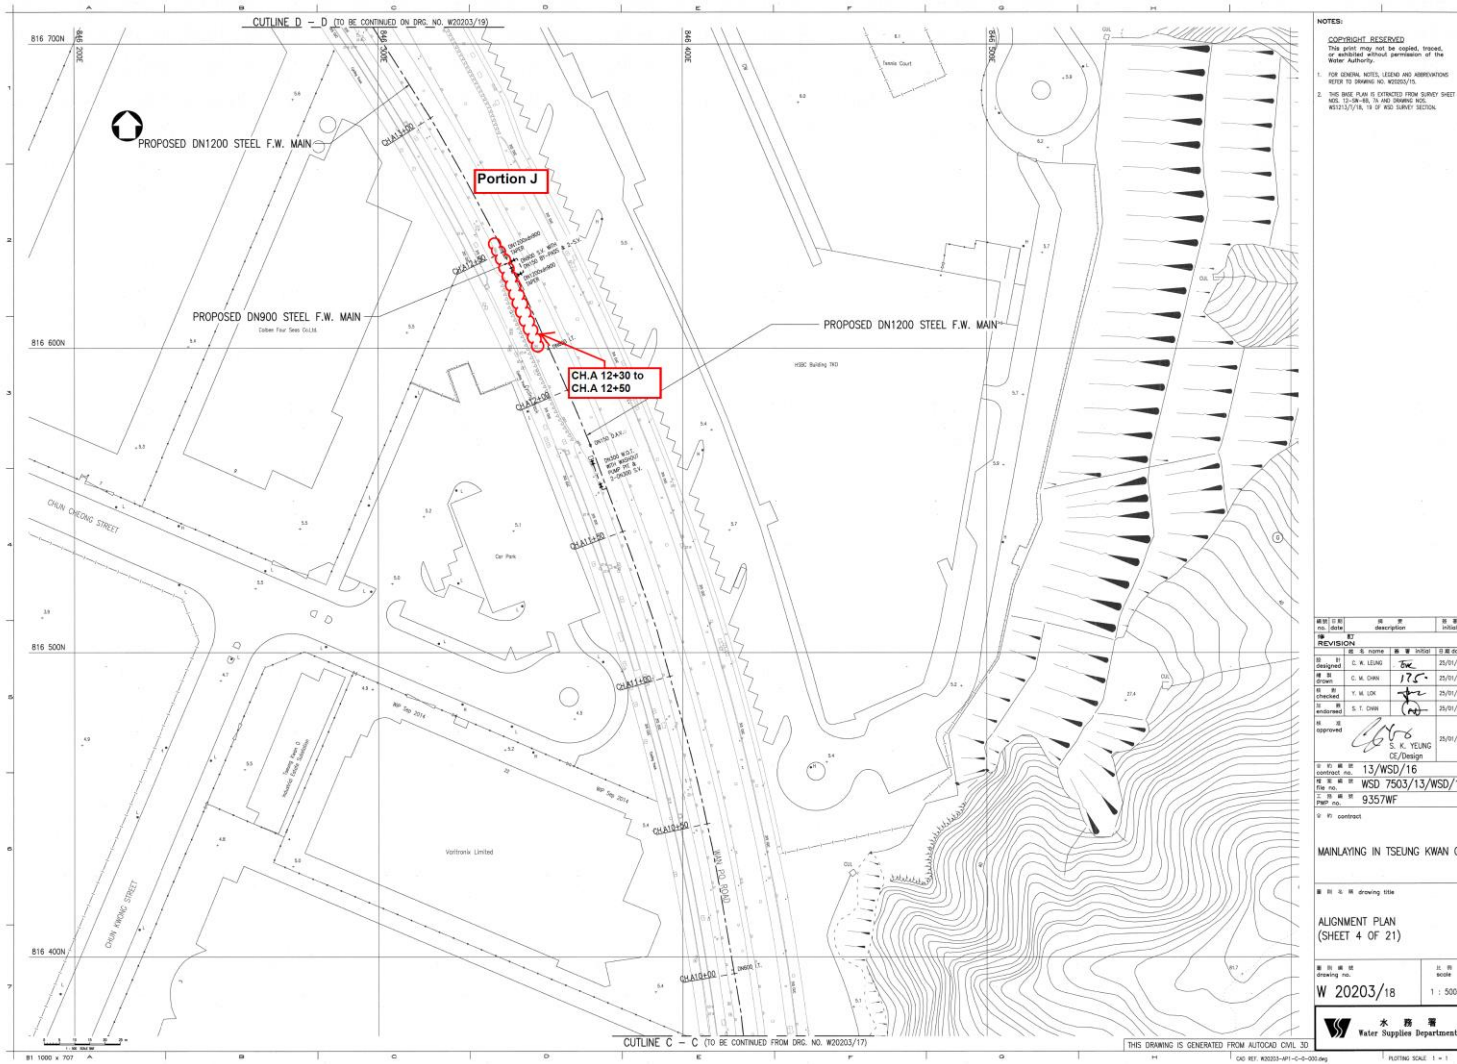

NOTES:

1. CONTRACT RESERVED. This plan may not be copied, traced, or amended without permission of the Water Authority.
2. FOR GENERAL NOTES, LEGEND AND ABBREVIATIONS REFER TO DRAWING NO. WSD001/15.
3. THIS BLUE PLAN IS EXTRACTED FROM SURVEY SHEET NO. 13-30-46, 13-40-30 AND 13-40-31, 13-40-32, 13-40-33, 13-40-34, 13-40-35, 13-40-36, 13-40-37, 13-40-38, 13-40-39, 13-40-40, 13-40-41, 13-40-42, 13-40-43, 13-40-44, 13-40-45, 13-40-46, 13-40-47, 13-40-48, 13-40-49, 13-40-50, 13-40-51, 13-40-52, 13-40-53, 13-40-54, 13-40-55, 13-40-56, 13-40-57, 13-40-58, 13-40-59, 13-40-60, 13-40-61, 13-40-62, 13-40-63, 13-40-64, 13-40-65, 13-40-66, 13-40-67, 13-40-68, 13-40-69, 13-40-70, 13-40-71, 13-40-72, 13-40-73, 13-40-74, 13-40-75, 13-40-76, 13-40-77, 13-40-78, 13-40-79, 13-40-80, 13-40-81, 13-40-82, 13-40-83, 13-40-84, 13-40-85, 13-40-86, 13-40-87, 13-40-88, 13-40-89, 13-40-90, 13-40-91, 13-40-92, 13-40-93, 13-40-94, 13-40-95, 13-40-96, 13-40-97, 13-40-98, 13-40-99, 13-40-100.

REVISED BY	DATE	DESCRIPTION	INITIAL
REVISION:			
1	25/01/17	DESIGNED	C. K. LING
2	25/01/17	CHECKED	T. M. LOK
3	25/01/17	APPROVED	S. T. CHAN
	25/01/17	DESIGNED	S. K. YELING

CONTRACT NO. 13/WSD/16  
 DRAWING NO. WSD 7503/13/WSD/16  
 DRAWING TITLE: MAINLAYING IN TSEUNG KWAN O  
 SHEET TITLE: ALIGNMENT PLAN (SHEET 4 OF 21)  
 DRAWING NO. W 20203/18  
 SCALE: 1:500  
 DEPARTMENT: Water Supplies Department

Figure B4. Location Plan for Portion J - CH.A 12+30 to CH.A 12+50


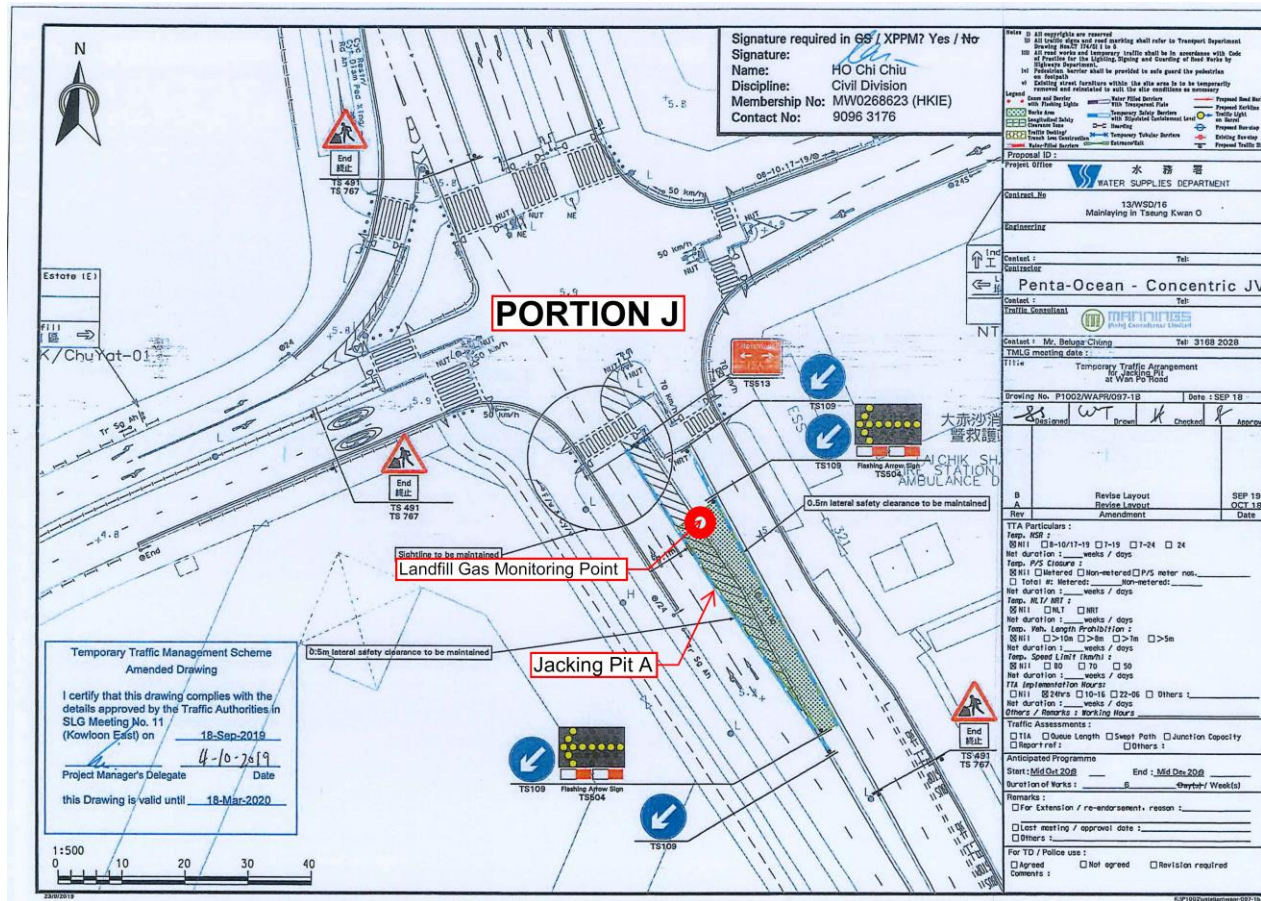


Figure B5. Location Plan for Portion J – CH. A13+50 to CH.A 14+00 (Pit A)

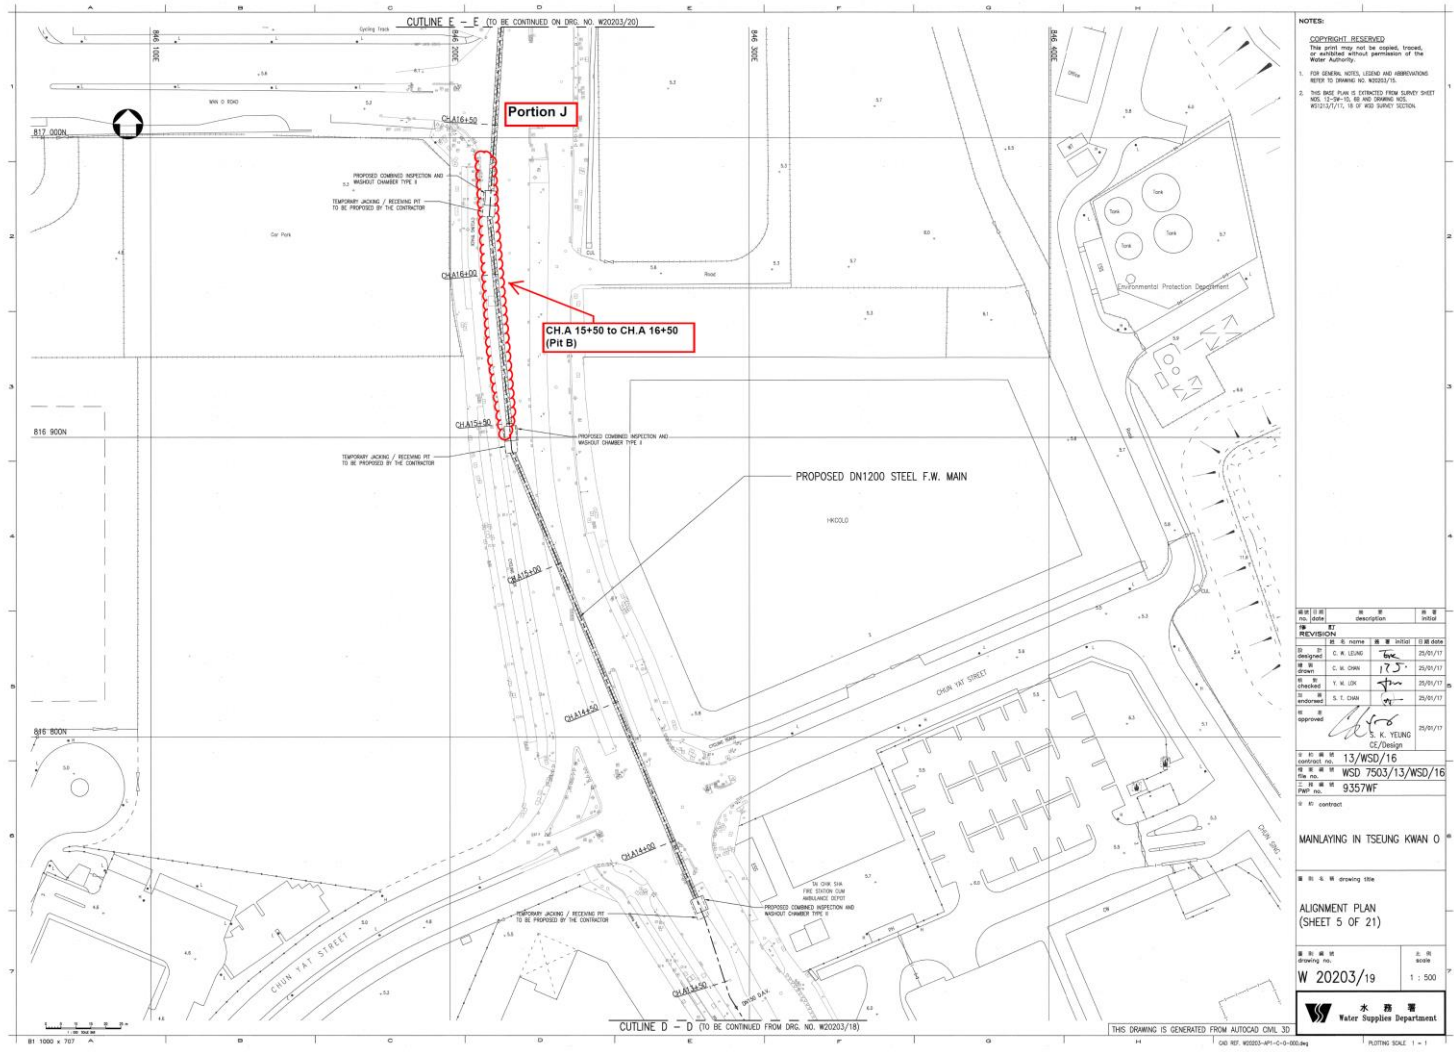

**Figure B6. Location Plan for Portion J – CH. A15+50 to CH.A 16+50 (Pit B)**

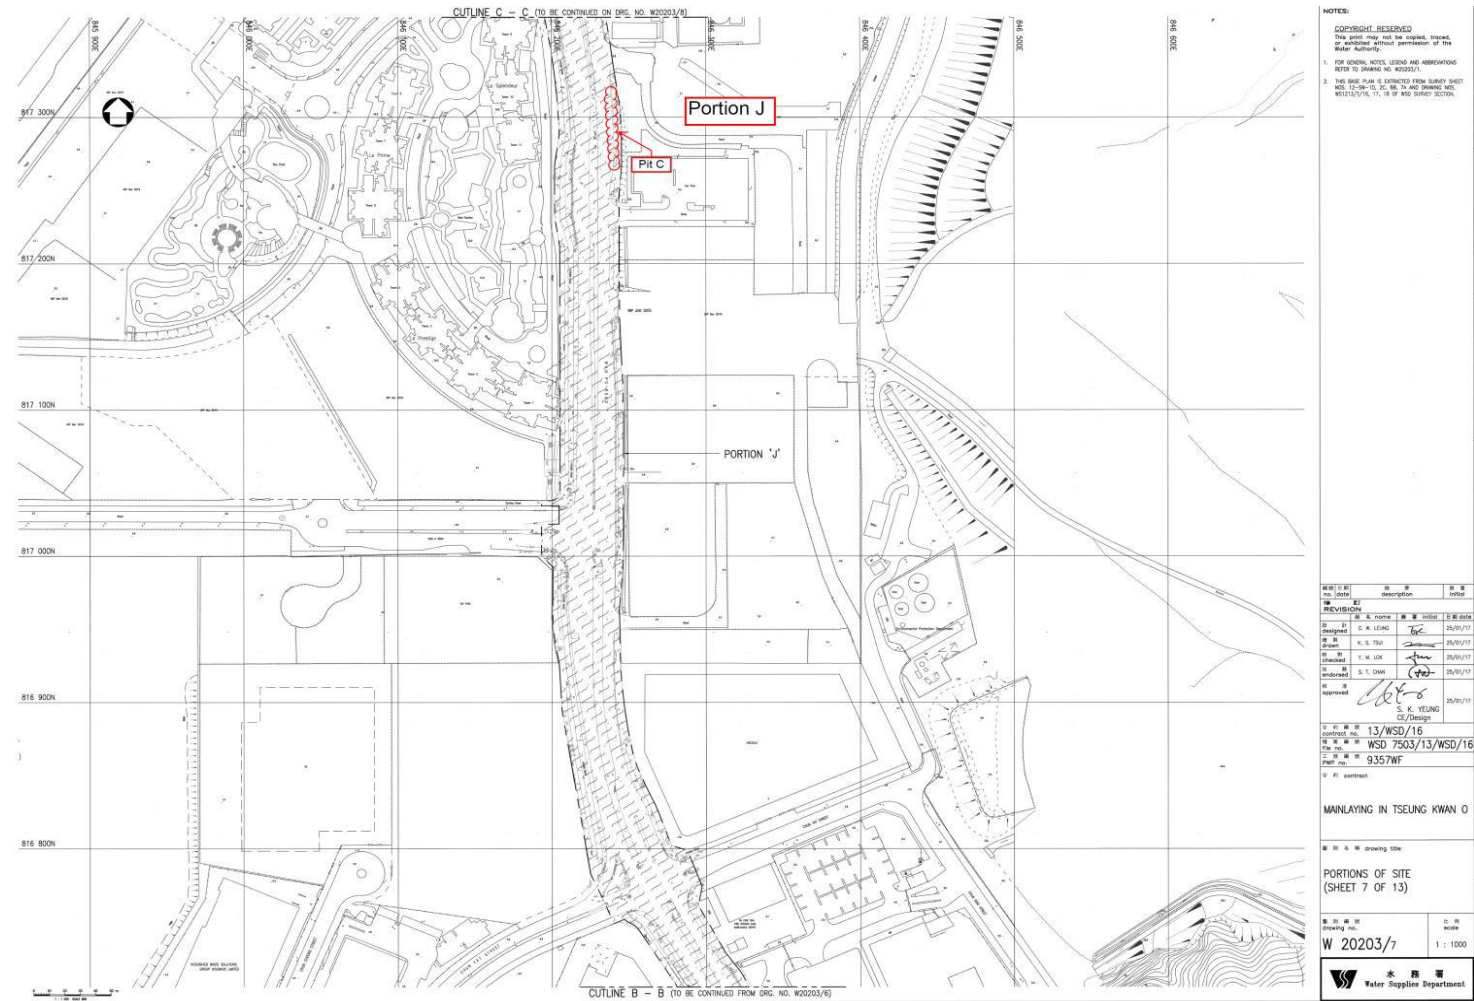


Figure B7. Location Plan for Portion J – CH.A 19+15 to CH.A 19+50 (Pit C)

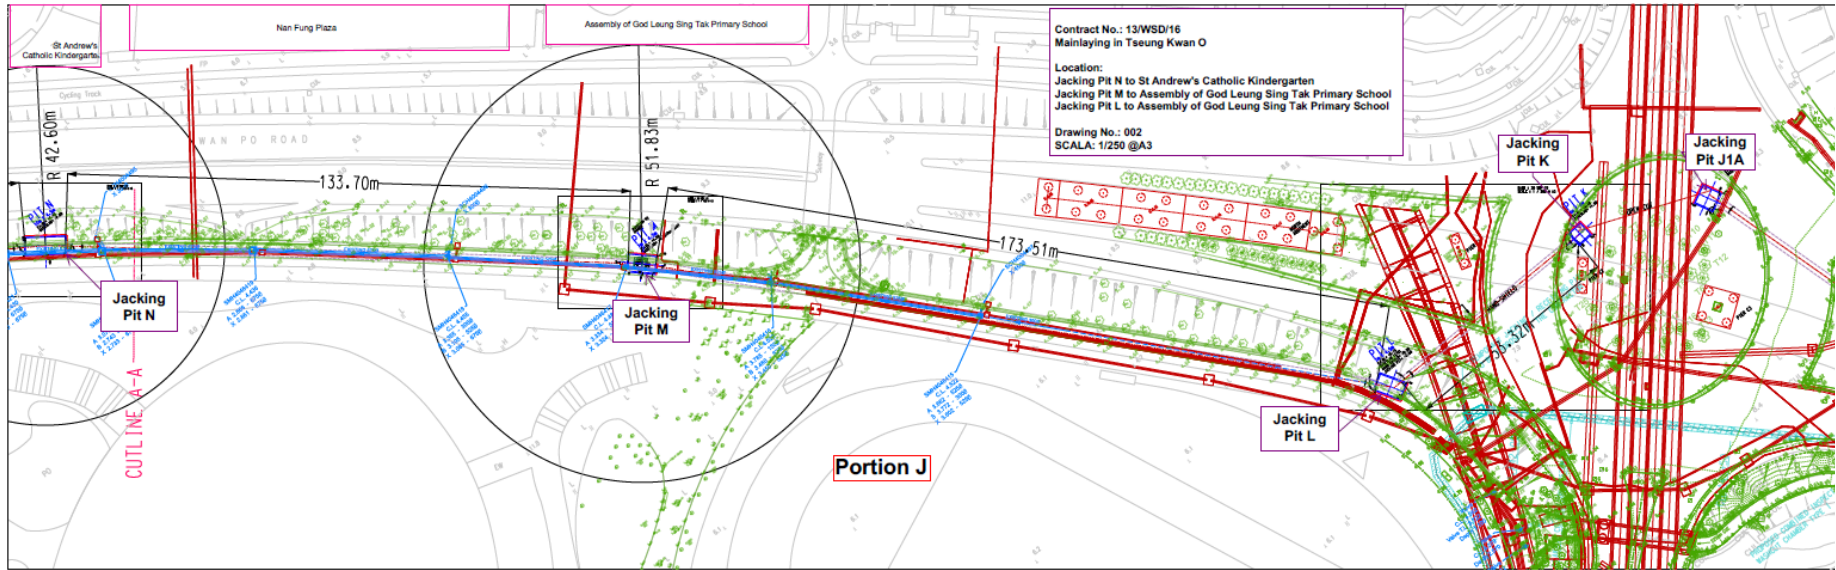


Figure B8a. Location Plan for Portion J – Pit L-M-N, K, J1A

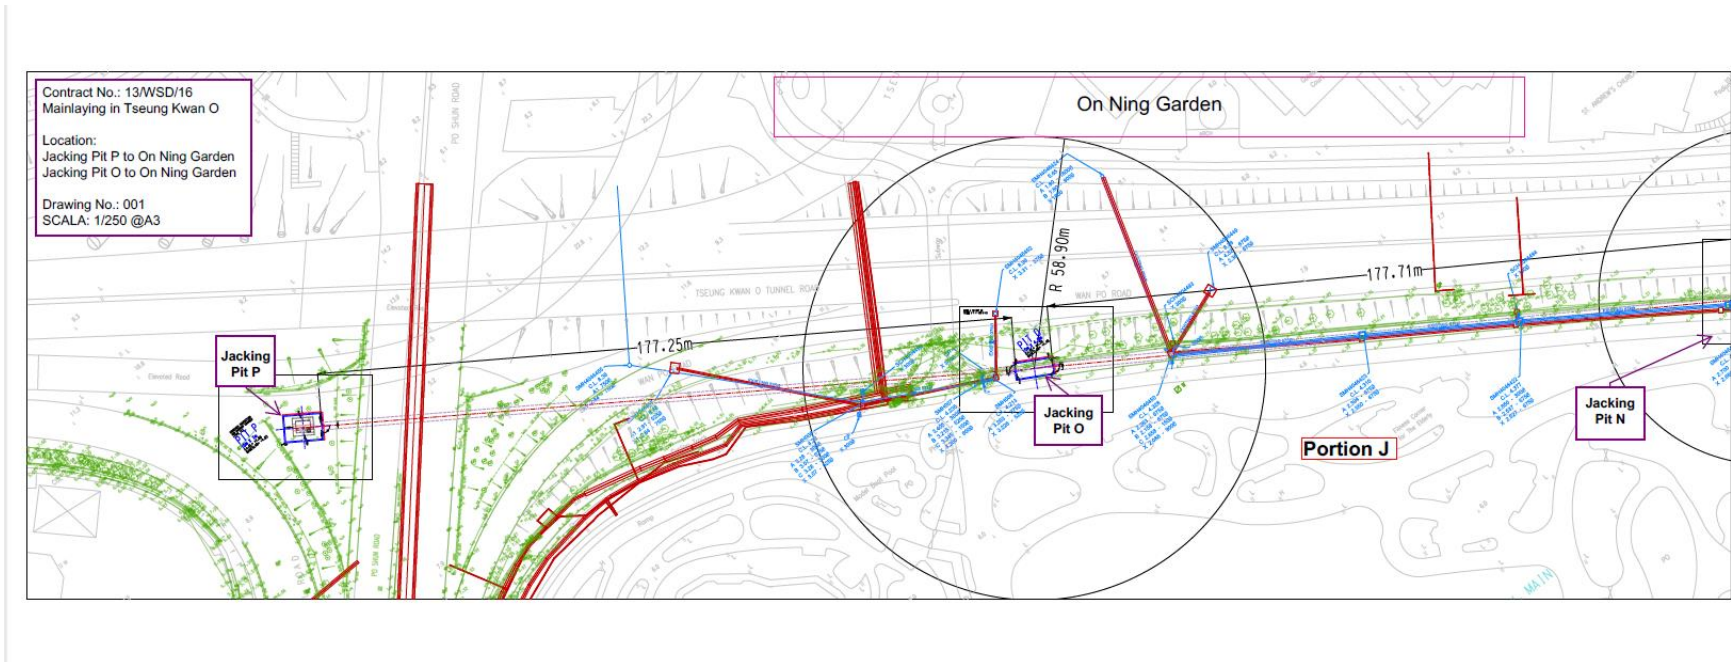


Figure B8b. Location Plan for Portion J – Pit N-O-P

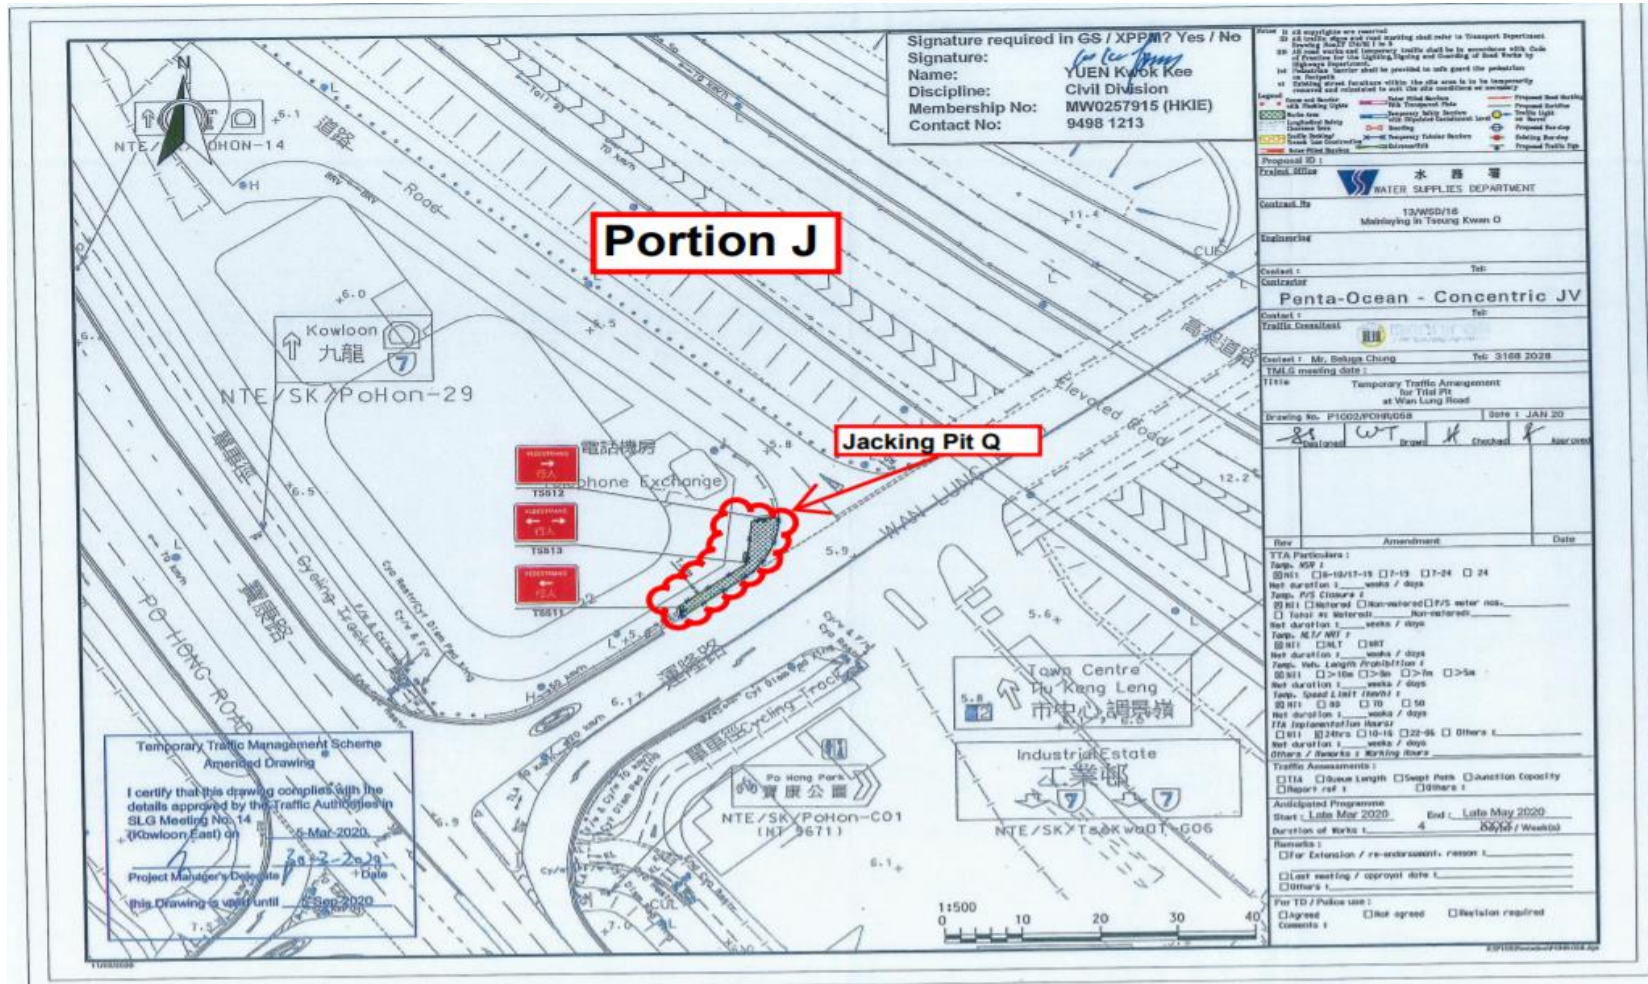


Figure B8c. Location Plan for Portion J – Pit Q



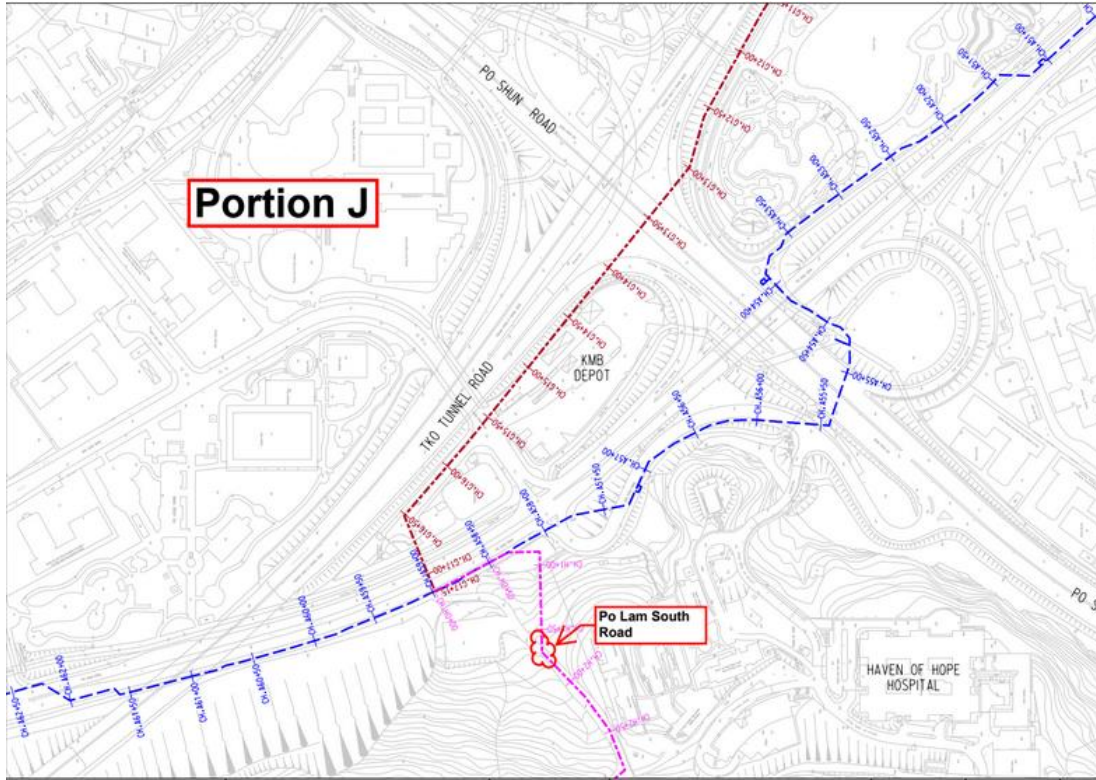


Figure B9a. Location Plan for Mau Wu Tsai 1

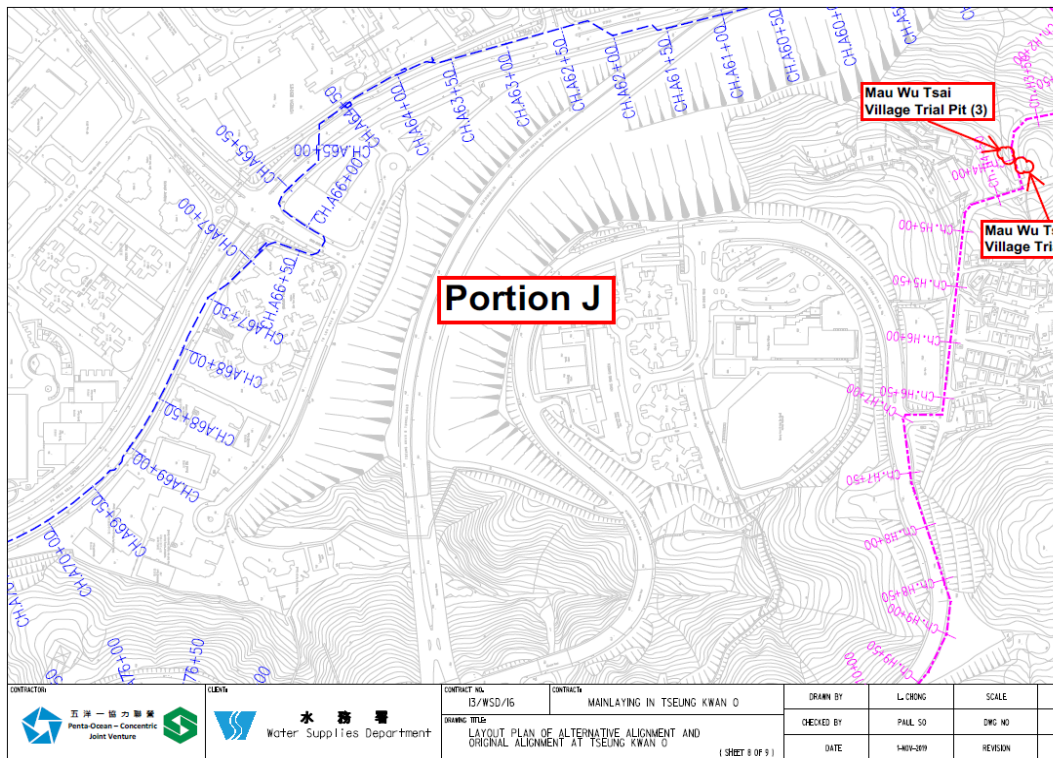


Figure B9b. Location Plan for Mau Wu Tsai 2 & 3

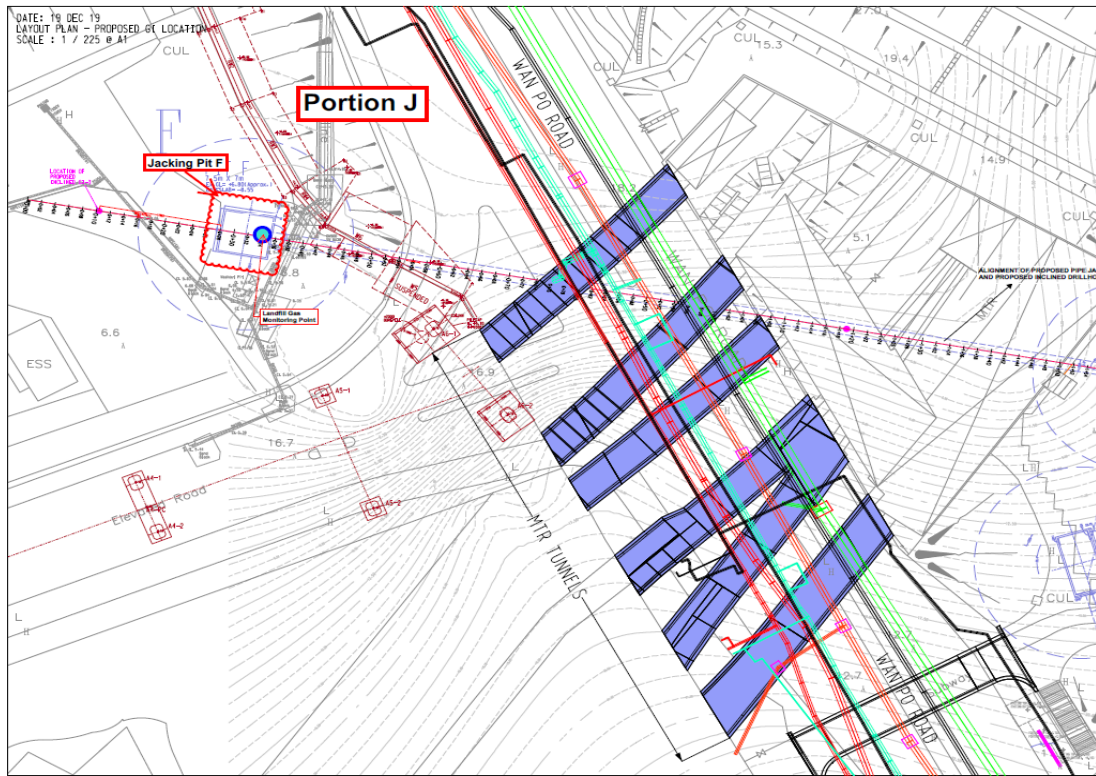


Figure B10. Location Plan for Jacking Pit F

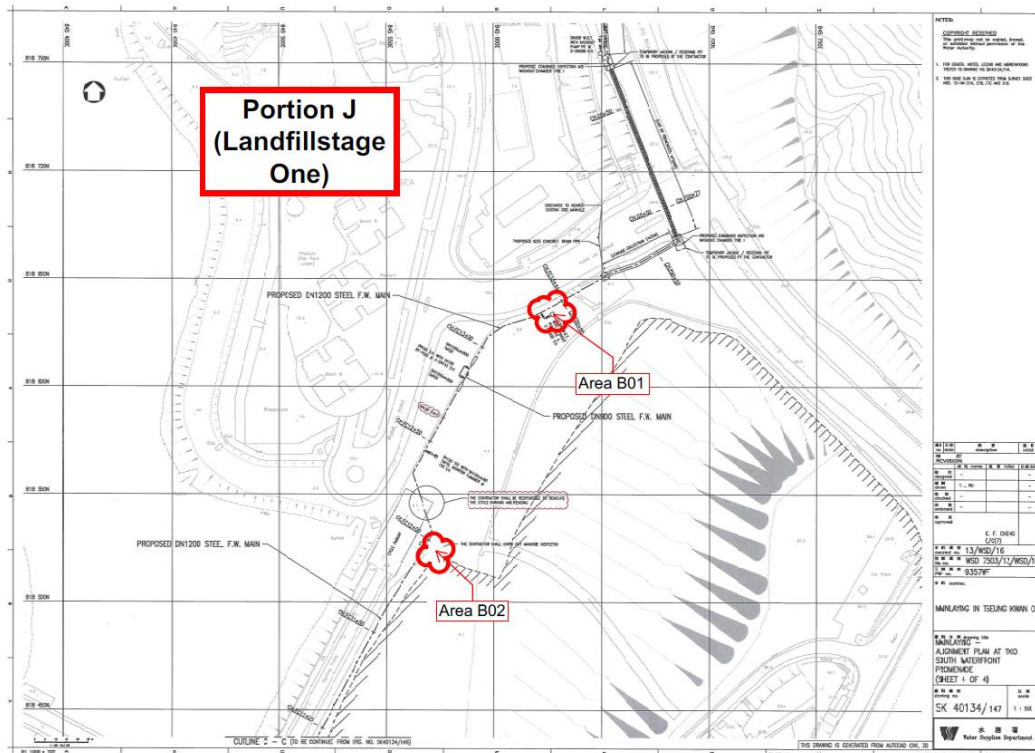


Figure B11a. Location Plan – Landfill Stage 1 (Area B01-B02)

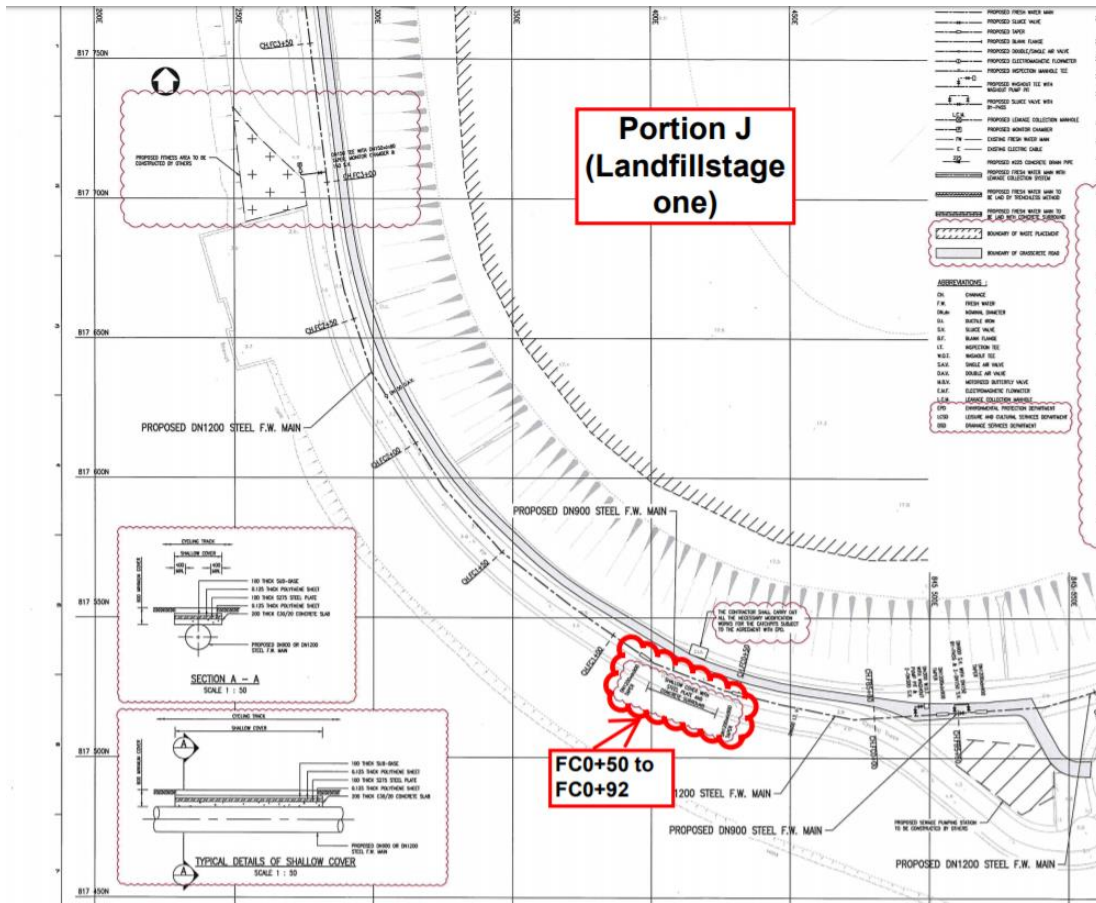


Figure B11b. Location Plan – Landfill Stage 1 (Area FC0+50 -FC0+92)

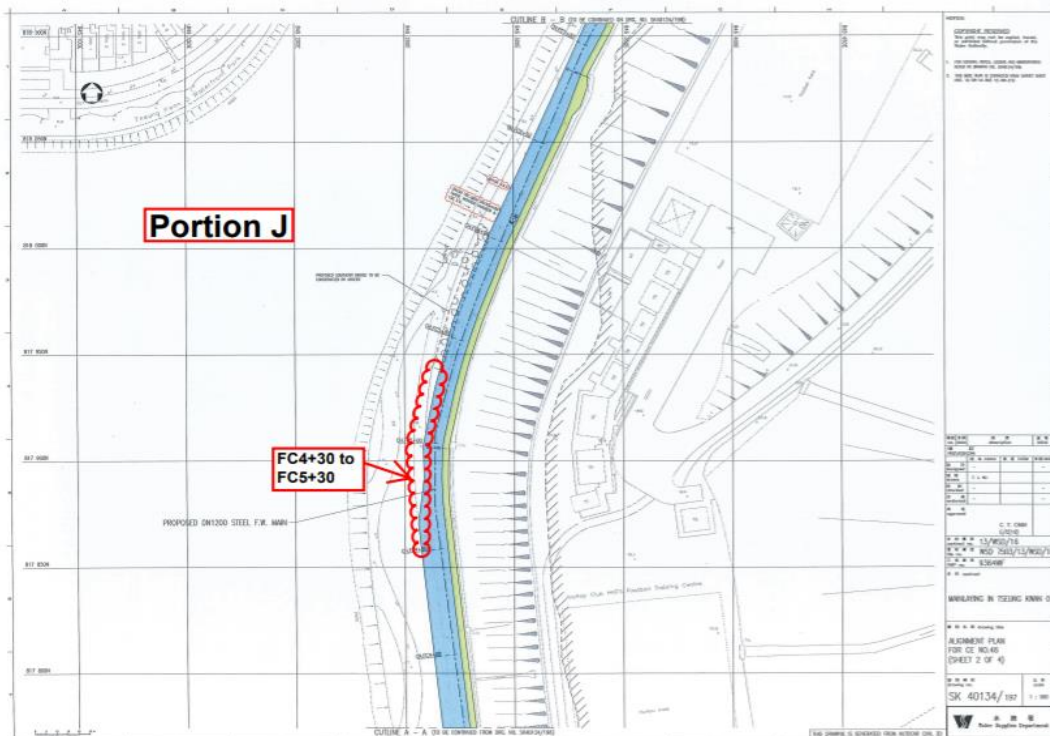


Figure B11c. Location Plan – Landfill Stage 1 (Area FC4+30 -FC5+30)

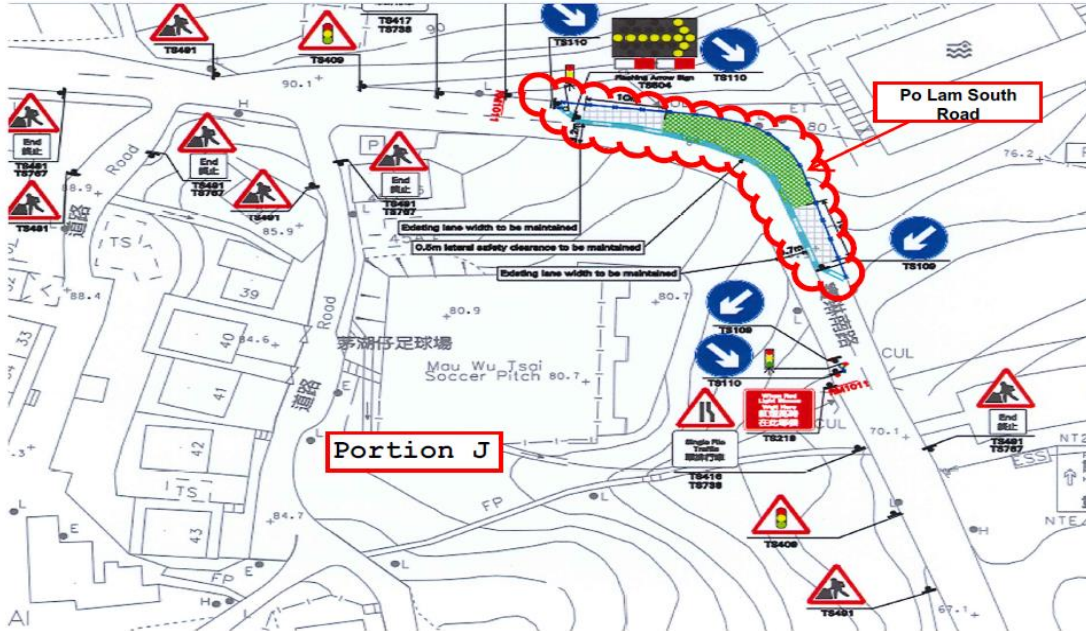


Figure B12. Monitoring Location – Po Lam South Road

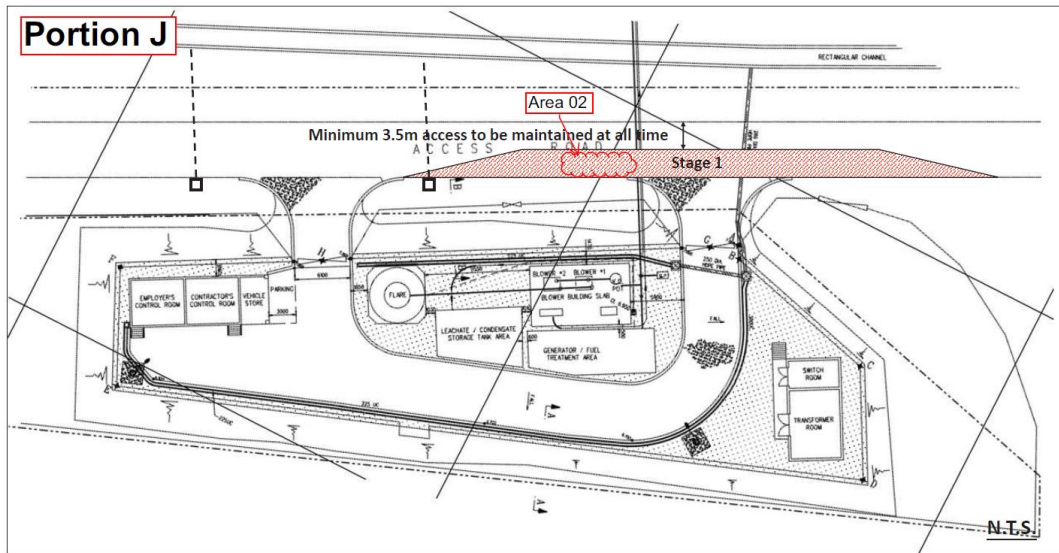


Figure B13. Monitoring Location – Area A02

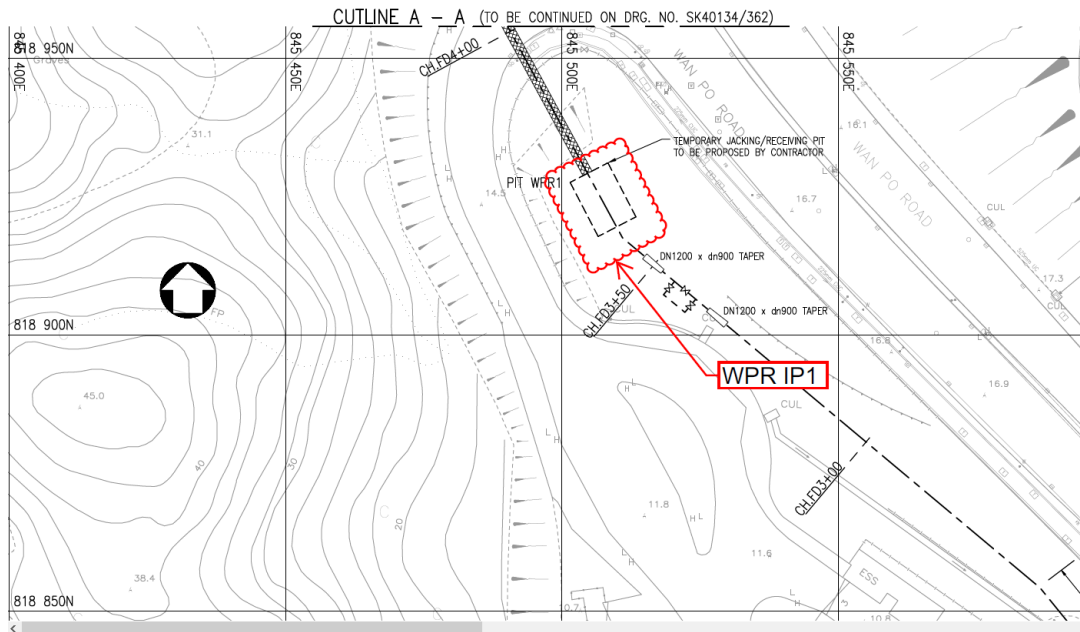


Figure B14. Location Plan for WPR IP1

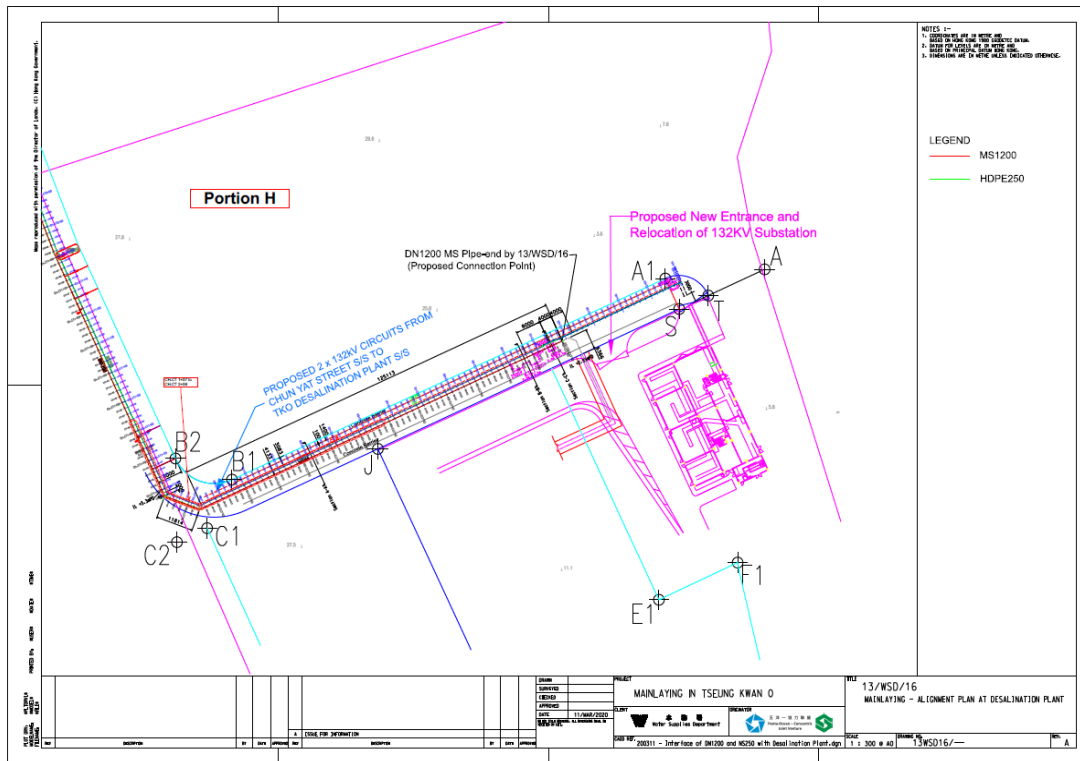


Figure B15a. Location Plan for CH.CT 0+07 - 2+58

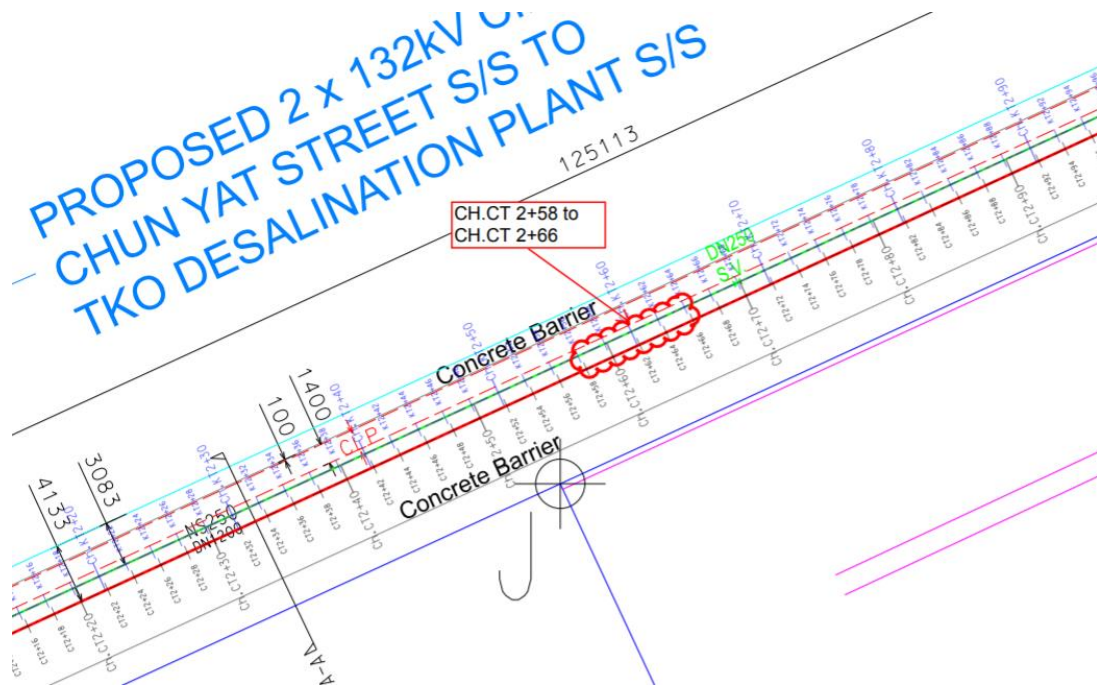


Figure B15b. Location Plan for CH.CT 2+58 – 2+66

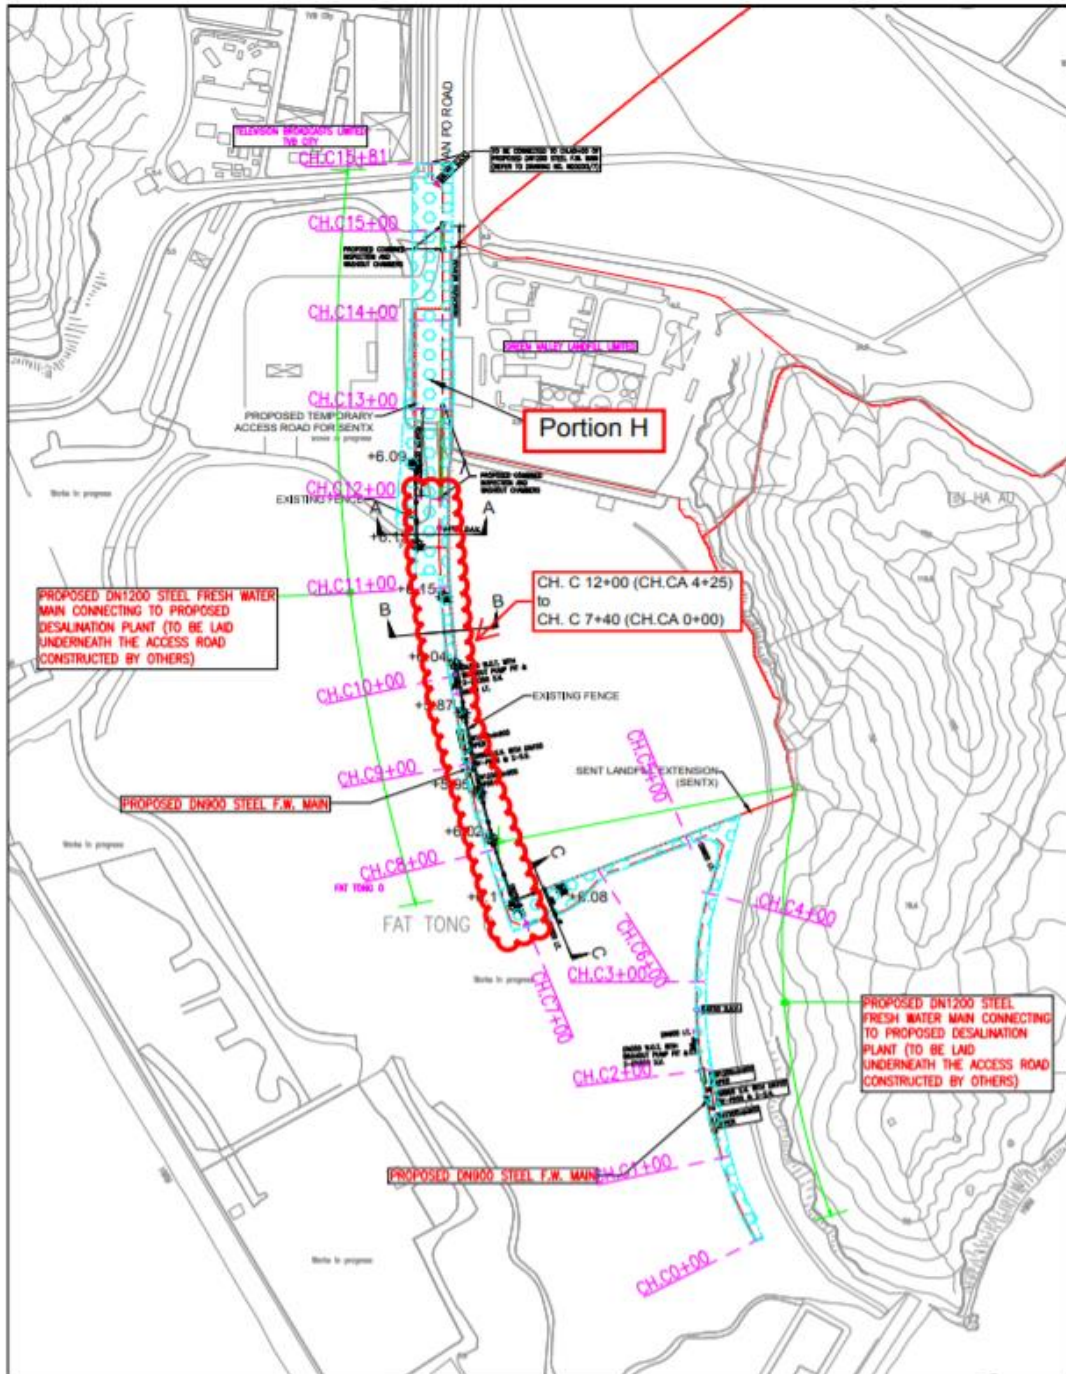


Figure B16. Location Plan for Portion H- CH.C 7+40~CH.C 12+00 (CH.CA 0+00 ~ CH.CA4+25)

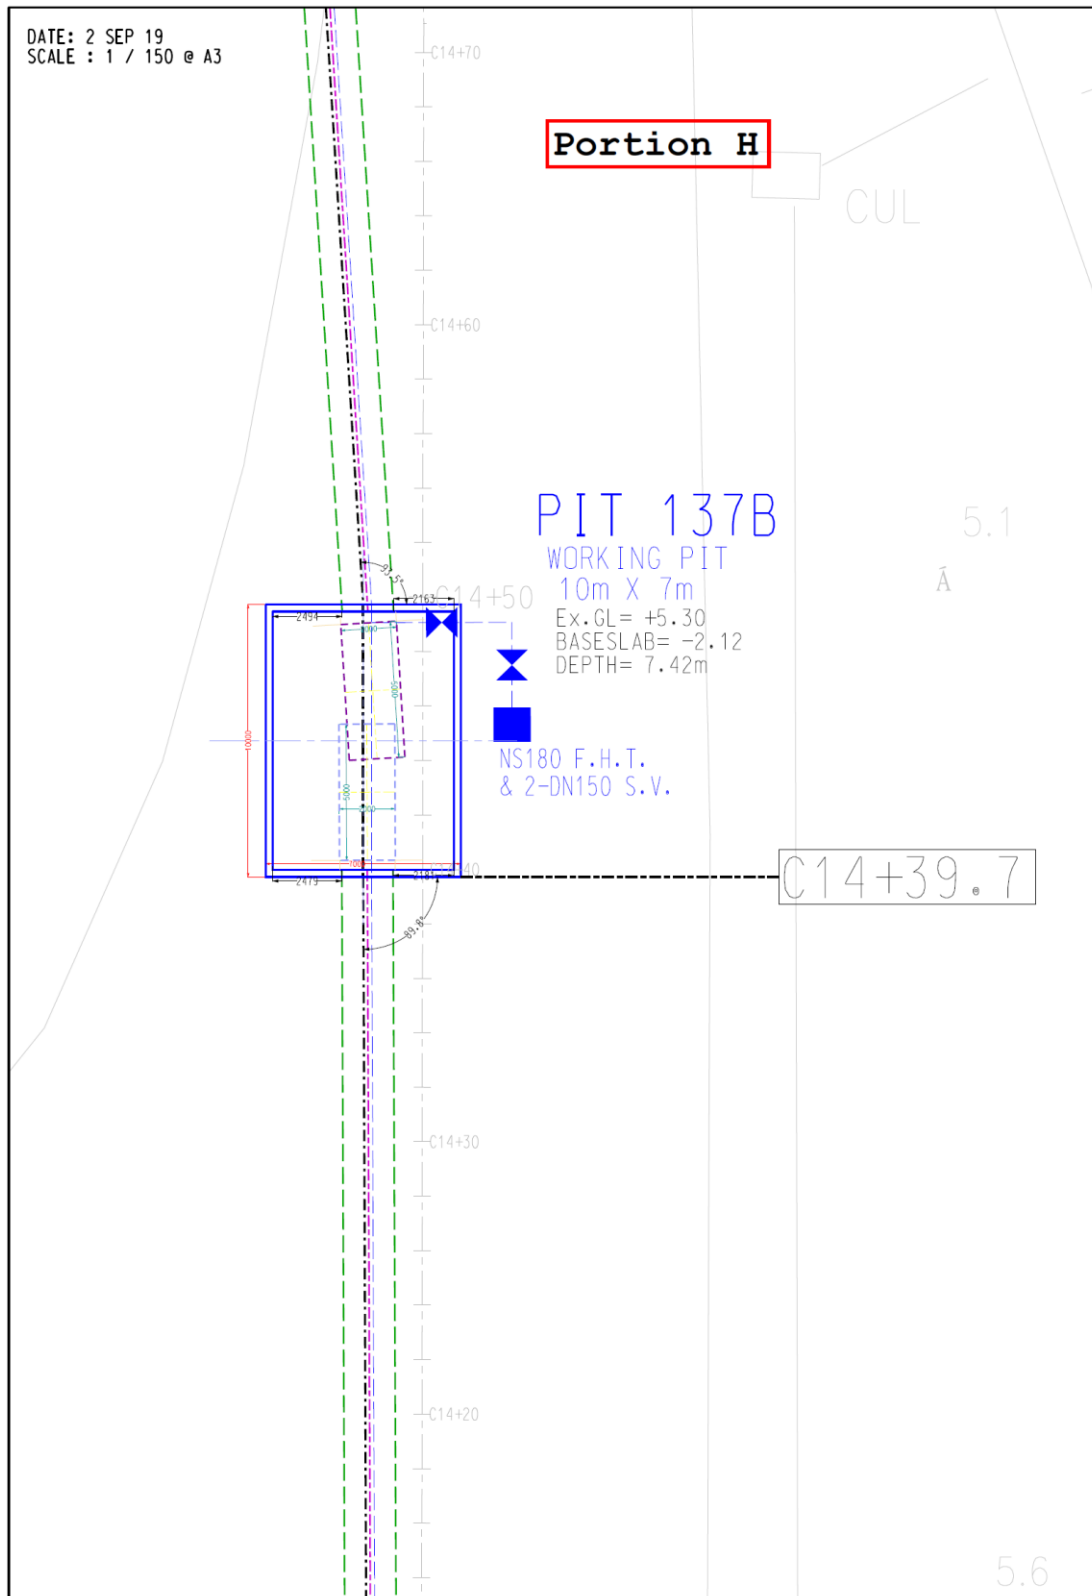


Figure B17a. Location Plan for Portion H- Pit 137B



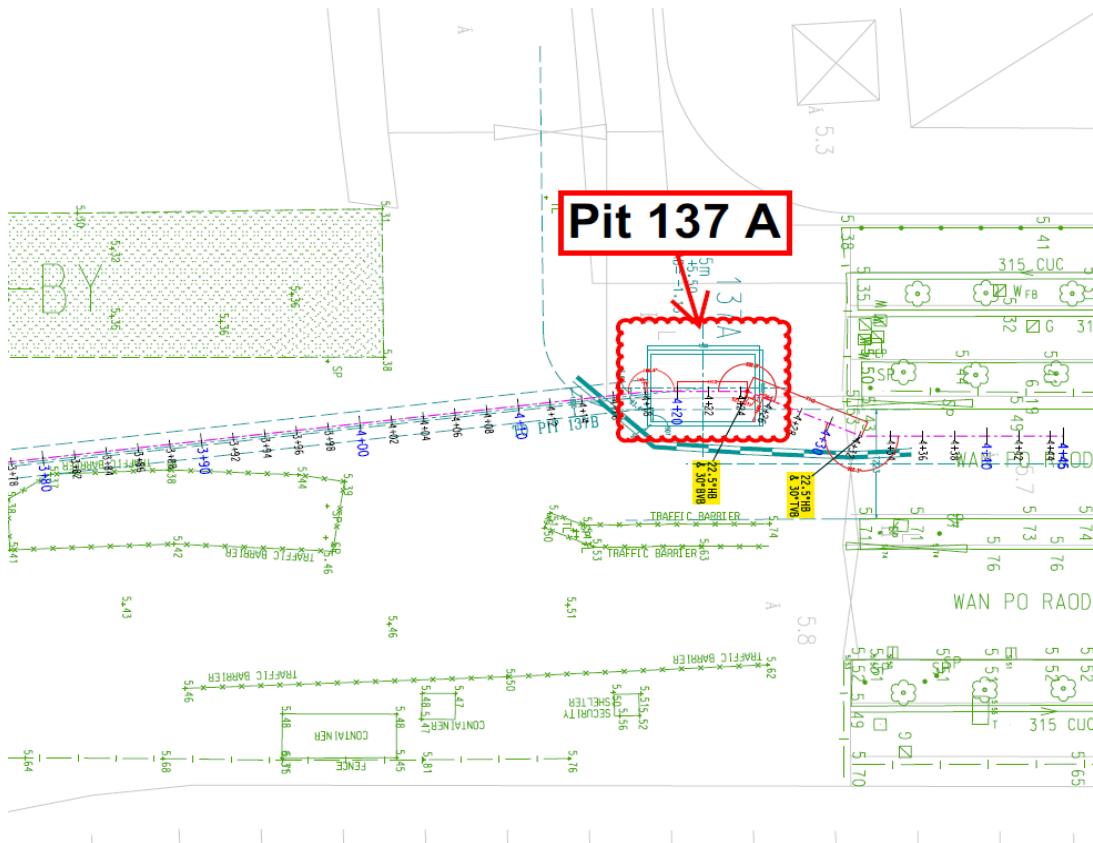


Figure B17b. Location Plan for Portion H- Pit 137A

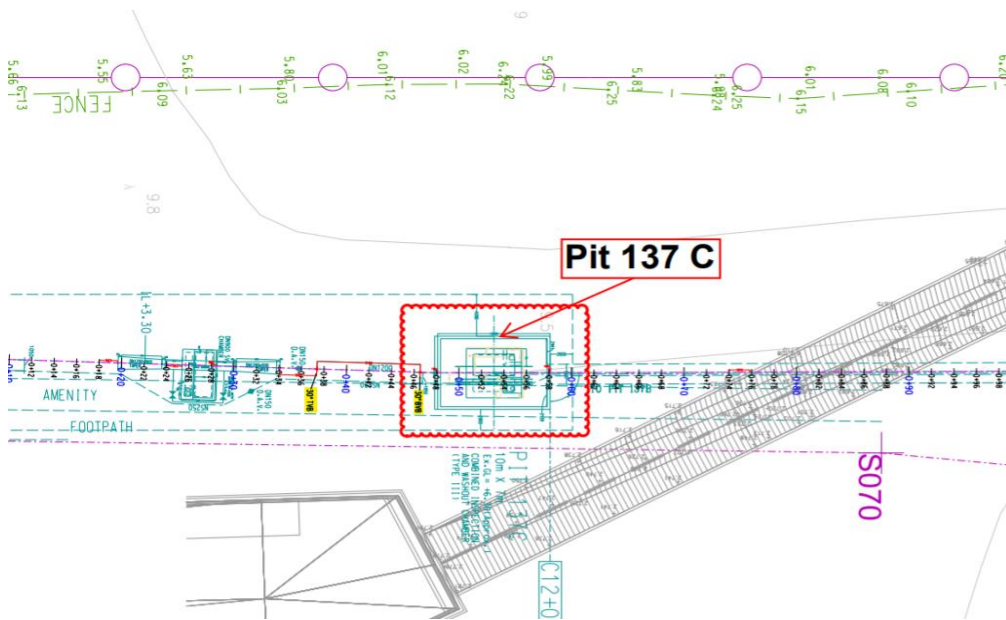


Figure B17c. Location Plan for Portion H- Pit 137C

## Appendix C

# Summary of Implementation Status of Environmental Mitigation

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
<b>Air Quality</b>								
S4.8.1	Impervious dust screen or sheeting will be provided to enclose scaffolding from the ground floor level of building for construction of superstructure of the new buildings.	Land site/ During Construction	Contractor(s)		✓		N/A	Air Pollution Control (Construction Dust)
S4.8.1	Impervious sheet will be provided for skip hoist for material transport.	Land site/ During Construction, particularly dry season	Contractor(s)		✓		NA	
S4.8.1	The area where dusty work takes place should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after dusty activities as far as practicable.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	All dusty materials should be sprayed with water or a dust suppression chemical immediately prior to any loading, unloading or transfer operation.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	Dropping heights for excavated materials should be controlled to a practical height to minimize the fugitive dust arising from unloading.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	During transportation by truck, materials should not be loaded to a level higher than the side and tail boards, and should be dampened or covered before transport.	Land site/ During Construction	Contractor(s)		✓		N/A	
S4.8.1	Wheel washing device should be provided at the exits of the work sites. Immediately before leaving a construction site, every vehicle shall be washed to remove any dusty material from its body and wheels as far as practicable.	Land site/ During Construction	Contractor(s)		✓		N/A	

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S4.8.1	Road sections between vehicle-wash areas and vehicular entrance will be paved.	Land site/ During Construction	Contractor(s)		✓		N/A	
S4.8.1	Hoarding of not less than 2.4m high from ground level will be provided along the length of the Project Site boundary.	Land site/ During construction	Contractor(s)	✓	✓		N/A	
S4.8.1	Haul roads will be kept clear of dusty materials and will be sprayed with water so as to maintain the entire road surface wet at all times.	Land site/ During construction	Contractor(s)		✓		Implemented, rectified after observation	
S4.8.1	Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets or sprayed with water to maintain the entire surface wet all the time.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.8.1	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.8.1	All exposed areas will be kept wet always to minimise dust emission.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.8.1	Ultra-low-sulphur diesel (ULSD) will be used for all construction plant on-site, as defined as diesel fuel containing not more than 0.005% sulphur by weight) as stipulated in Environment, Transport and Works Bureau Technical Circular (ETWB-TC(W)) No 19/2005 on Environmental Management on Construction Sites.	Land site/ During construction/ During Operation	Contractor(s)		✓	✓	Implemented	Environment, Transport and Works Bureau Technical Circular (ETWB-TC(W)) No 19/2005 on Environmental Management on Construction Sites

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S4.8.1	The engine of the construction equipment during idling will be switched off.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.8.1	Concrete batching plant will be required on site. control measures recommended in the Guidance Note on a Best Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be implemented. The control measures recommended in the Guidance Note on a Best Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be	Land site/ During construction	Contractor(s)		✓		N/A	Guidance Note on a Best
S4.8.1	Regular maintenance of construction equipment deployed on-site will be conducted to prevent black smoke emission.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.10	To ensure proper implementation of the recommended dust mitigation measures and good construction site practices during the construction phase, environmental site audits on weekly basis is recommended throughout the construction period.	Land site/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	

Note: D – Design stage C – Construction O – Operation

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
<b>Noise</b>								
S5.7	Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase.	All area/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Mobile plant, if any, will be sited as far away from NSRs as possible.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Plants known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Use of Quiet Powered Mechanical Equipment (QPME).	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Movable noise barriers of 3m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
	than its height. The noise barrier material should have a superficial surface density of at least 7 kg m <sup>-2</sup> and have no openings or gaps.							
S5.7	The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Construction activities (e.g. excavation/shoring, reinstatement (asphalt), and pipe jacking) will be planned and carried out in sequence, such that items of PME proposed for these activities will not be operated simultaneously.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works
S5.7	PMEs will not be used at the works areas near educational institutions with residual impact (ie the "influence area" within a radius of 40m) during school hours in order to reduce impact to the educational institutions.	Noise control / During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works
S5.7	Noise enclosures or acoustic sheds would be used to cover stationary PME such as generators. Portable/Movable noise enclosure made of material with superficial surface density of at least 7 kg m <sup>-2</sup> may be used for screening the noise from operation of the saw/groover, concrete.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		N/A	
S5.9	Sawcutting pavement, breaking up of pavement, excavation /shoring, pipe laying, backfilling, reinstatement (concrete) and pipe jacking shall be scheduled outside the examination period.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		Implemented	

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S5.9	In view the duration of noise exceedance at Creative Secondary School, PLK Laws Foundation College, TKO Kei Tak Primary School and School of Continuing and Professional Studies-CUHK is limited to 8 weeks, the construction work in the influence areas near the four schools shall be scheduled during long school holidays (eg summer holiday, Easter holiday or Christmas holiday, etc) as far as practicable. Scheduling the construction work for the four schools.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		Implemented	
S5.10	A noise monitoring programme shall be implemented for the construction phase.	Designated monitoring stations as defined in EM&A Manual/During construction phase	Environmental Team (ET)		✓		Implemented	
S5.10	The effectiveness of on-site control measures could also be evaluated through the regular site audits.	All facilities/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	-

Note: D – Design stage C – Construction O – Operation



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementati on Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
<b>Water Quality</b>								
S6.9	Dredged marine sediment will be disposed of in a gazetted marine disposal area in accordance with marine dumping permit conditions of the Dumping at Sea Ordinance (DASO).	Marine Dredging/ During construction	Contractor(s)		✓		N/A	Dumping at Sea Ordinance (DASO)
S6.9	Disposal vessels will be fitted with tight bottom seals in order to prevent leakage of material during transport.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	Barges will be filled to a level, which ensures that material does not spill over during transport to the disposal site and that adequate freeboard is maintained to ensure that the decks are not washed by wave action.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	After dredging, any excess materials will be cleaned from decks and exposed fittings before the vessel is moved from the dredging area.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	All vessels should be well maintained and inspected before use to limit any potential discharges to the marine environment.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	All vessels must have a clean ballast system.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	No discharge of sewage/grey wastewater should be allowed. Waste water from potentially contaminated area on working vessels should be minimized and collected. These kinds of wastewater should be brought back to port and discharged at appropriate collection and treatment system.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	No soil waste is allowed to be disposed overboard.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementati on Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.9	Silt removal facilities such as silt traps or sedimentation facilities will be provided to remove silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities will be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented, rectified after observation	ProPECC PN 1/94 TM Standard under the WPCO
S6.9	Earthworks to form the final surfaces will be followed up with surface protection and drainage works to prevent erosion caused by rainstorms.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9	Appropriate surface drainage will be designed and provided where necessary.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9	The precautions to be taken at any time of year when rainstorms are likely together with the actions to be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	ProPECC PN 1/94
S6.9	Oil interceptors will be provided in the drainage system where necessary and regularly emptied to prevent the release of oil and grease into the storm water drainage system after accidental spillages.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented, rectified after observation	-
S6.9	Temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge, if any, will be adequately designed for the controlled release of storm flows.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.9	The temporary diverted drainage, if any, will be reinstated to the original condition when the construction work has finished or when the temporary diversion is no longer required.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-
S6.9	Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the construction workers over the construction site to prevent direct disposal of sewage into the water environment.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9 and S6.12	The sterilization water should be dechlorinated with total residual chlorine (TRC) level below 1 mg/L before discharge to public sewer. In situ testing of TRC should also be conducted for the discharge of chlorinated water for pipeline disinfection to ensure sufficient dechlorination before discharge to public sewer.	Sterilization of water mains prior to commissioning	Contractor(s)		✓	✓	N/A	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	The cleaning and flushing water should also be treated and desilted to the relevant discharge requirement stipulated in TM-DSS before discharging.	Sterilization of water mains prior to commissioning	Contractor(s)		✓	✓	N/A	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	Site drainage should be well maintained and good construction practices should be observed to ensure that oil, fuels, solvents and other chemicals are managed, stored and handled properly and do not enter the nearby water streams.	Land site & drainage/ During construction/ During operation	Contractor(s)		✓	✓	Implemented, rectified after observation	-

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.12	Regular site inspections will be carried out in order to confirm that regulatory requirements are being met and that contractors are implementing the standard site practice and mitigation measures as proposed to reduce potential impacts to water quality.	During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	-

Note: D – Design stage C – Construction O – Operation

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
<b>Waste Management</b>								
S8.5	Nomination of approved personnel to be responsible for standard site practices, arrangements for collection and effective disposal to an appropriate facility of all wastes generated at the site.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Training of site personnel in proper waste management and chemical handling procedures. Training will be provided to workers on the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling at the beginning of the construction works.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Provision of sufficient waste disposal points and regular collection for disposal.	All area/ During construction/ During operation	Contractor(s)		✓	✓	Implemented	DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	Appropriate measures to reduce windblown litter and dust transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	All area/ During construction	Contractor(s)		✓		Implemented, rectified after reminder.	DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	A waste management plan (WMP) as stated in the "ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites" for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established and implemented during the construction phase as part of the Environmental Management Plan (EMP). The Contractor will be required to prepare the EMP and submits it to the Architect/ Engineer under the Contract for approval prior to implementation.	All area/ During construction	Contractor(s)		✓		Implemented	ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites
S8.5	Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Centre at Tsing Yi.	All area/ During construction	Contractor(s)		✓		N/A	Chapters 2 & 3 Code of Practice on the Packaging Labelling & Storage of

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
								Chemical Wastes published under the Waste Disposal Ordinance (Cap 354), Section 35
S8.5	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.	Land site/ During construction	Contractor(s)		✓		Implemented, rectified after observation	Waste Disposal Ordinance (Cap 354)
S8.5	A recording system for the amount of wastes generated/ recycled and disposal sites. The trip-ticket system will be included as one of the contractual requirements and implemented by the contractor(s).	Land site/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of material and their proper disposal.	Land site/ During construction/ During operation	Contractor(s)		✓		Implemented	WBTC 32/92, The Use of Tropical Hard Wood on Construction Site
S8.5	Encourage collection of aluminium cans and waste paper by individual collectors during construction with separate labelled bins provided to segregate these wastes from other general refuse by the workforce.	Land site/ During construction	Contractor(s)		✓		Implemented	ETWB TCW No. 33/2002, Management of Construction and Demolition Material Including Rock
S8.5	Any unused chemicals and those with remaining functional capacity will be recycled as far as possible.	Land site/ During construction	Contractor(s)		✓		N/A	-
S8.5	Use of reusable non-timber formwork to reduce the amount of C&D materials.	All areas/ During construction	Contractor(s)		✓		N/A	WBTC 32/92, The Use of Tropical Hard Wood on Construction Site
S8.5	Prior to disposal of construction waste, wood, steel and other metals will be separated to the extent practical, for re-use and/or recycling to reduce the quantity of waste to be disposed of to landfill.	All areas/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Proper storage and site practices to reduce the potential for damage or contamination of construction materials.	All areas/ During construction	Contractor(s)		✓		Implemented, rectified after observation	-

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	Plan and stock construction materials carefully to reduce amount of waste generated and avoid unnecessary generation of waste.	All areas/ During construction	Contractor(s)		✓		Implemented	-
S8.5	A Sediment Quality Report (SQR) for sampling and chemical testing of the sediment will be prepared and submitted to the EPD for approval. The approved detailed sampling and chemical testing will be carried out prior to the commencement of the dredging activities to confirm the sediment disposal method.	Marine works/ During construction	Contractor(s)		✓		N/A	ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The management of dredged/ excavated sediment management requirement from <i>ETWB TC(W) No. 34/2002</i> will be incorporated in the Specification of the Contract Documents.	Marine works/ During construction	WSD/ Contractor(s)		✓		Implemented	ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The contractor will open a billing account with EPD in accordance with the Waste Disposal (Charges for Disposal of Construction Waste) Regulation for the payment of disposal charges.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	Cap 354N Waste Disposal (Charges for Disposal of Construction Waste) Regulation
S8.5	A trip-ticket system will be established in accordance with DEVB TC(W) No. 6/2010 to monitor the reuse of surplus excavated materials off-site and disposal of construction waste and general refuse at transfer facilities/ landfills, and to control fly-tipping.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	The project proponent will also conduct regular inspection of the waste management measures implemented on site as described in the Waste Management Plan.	All area/ During construction	Contractor(s) / Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	A recording system (similar to summary table as shown in Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005) for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established during the construction phase.	All area/ During construction	Contractor(s)		✓		Implemented	Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005
S8.5	Inert C&D materials (public fill) will be reused within the Project as far as practicable.	All area/ During construction	Contractor(s)		✓		N/A	-
S8.5	Public fill and construction waste shall be segregated and stored in different containers or skips to facilitate reuse or recycling of materials and their proper disposal.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	To reduce the potential dust and water quality impacts of site formation works, C&D materials will be wetted as quickly as possible to the extent practice after filling.	All area/ During construction	Contractor(s)		✓		Implemented	Air Pollution Control (Construction Dust) Regulation (Cap 311R); WPCO (Cap 358)
S8.5	Open stockpiles of excavated/ fill materials or construction wastes on-site should be covered with tarpaulin or similar fabric.	Land site/ During Construction, particularly dry season	Contractor(s)		✓		Implemented	Air Pollution Control (Construction Dust) Regulation (Cap 311R)
S8.5	Chemical waste container shall be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Chemical waste container shall have a capacity of less than 450 L unless the specifications have been approved by the EPD.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	A label in English and Chinese shall be displayed on the chemical container in accordance with instructions prescribed in Schedule 2 of the Regulations.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be enclosed on at least 3 sides.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall have adequate ventilation.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary).	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be	All area/ During	Contractor(s)/		✓	✓	Implemented	Waste Disposal

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	arranged so that incompatible materials are appropriately separated.	construction/ During operation	WSD					(Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	General refuse will be stored in enclosed bins or compaction units separately from construction and chemical wastes.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Adequate number of waste containers will be provided to avoid over-spillage of waste.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	DEVB TC(W) No. 8/2010 Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	A reputable waste collector will be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimise odour, pest and litter impacts.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	-
S8.5	Recycling bins will be provided at strategic locations within the Site to facilitate recovery of recyclable materials (including aluminium can, waste paper, glass bottles and plastic bottles) from the Site. Materials recovered will be sold for recycling.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	-
S8.5	To avoid any odour and litter impact, accurate number of portable toilets will be provided for workers on-site.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	The burning of refuse on construction sites is prohibited by law.	All area/ During construction	Contractor(s)		✓		Implemented	Air Pollution Control Ordinance (Cap 311)
S8.7	To facilitate monitoring and control over the contractors' performance on waste management, a waste inspection and audit	All facilities/ During construction	ET/ IEC		✓		Implemented	-

**Contract No. 13/WSD/16  
Mainlaying in Tseung Kwan O  
Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	programme will be implemented throughout the construction phase.							

Note: D – Design stage C – Construction O – Operation

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
<b>Ecology</b>								
S9.7	For slope mitigation works within the Clear Water Bay Country Park, to avoid tree felling and damages to trees, the exact locations of the flexible barrier foundation plates, soil nails and rock dowels can be adjusted during detailed design, and a setback distance from existing trees is recommended to be maintained as far as practical. A detailed specification describing the exact locations of the flexible barrier foundation plates, soil nails and rock dowels will be prepared to illustrate how the setback distance from existing trees would be implemented for tree avoidance.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		Implemented	-
S9.7	Pruning of tree canopies along the alignment of the flexible barriers shall be limited to a minimum.	Slope mitigation works area/ During construction	Contractor(s)		✓		Implemented	
S9.7	The alignment of flexible barriers shall be optimized to preserve all species of conservation interest and minimize the impact to the existing vegetation as far as practicable. All individuals of <i>Marsdenia lachnostoma</i> within the slope mitigation areas shall be retained <i>in-situ</i> , by positioning the alignment of flexible barrier at a minimum 1.5m in a radius away from these individuals.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		N/A	-
S9.7 and 9.10	At the detailed design stage prior to the commencement of the slope mitigation works, a vegetation survey shall be carried out at the slope mitigation areas within the Clear Water Bay Country Park to assess the condition and identify the location of each individual of <i>Marsdenia lachnostoma</i> and other flora species of conservation interest that may be directly affected by the construction works.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		N/A	-
S9.7	Temporary fencing will be installed to fence off	Slope mitigation works	Contractor(s)		✓		N/A	-

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	the concerned species either in groups of individually within the works area and in the close proximity to prevent from being damaged and disturbed during construction. A sign identifying the site shall be attached to the fence and flagging tape shall be attached to the individuals to visualize their locations.	area/ During construction						
S9.7 and S9.10	A specification for fencing and demarcating individuals of <i>Marsdenia lachnostoma</i> (or other flora species of conservation interest, if found) adjacent to the proposed alignment of the flexible barriers will be prepared to protect the species.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Induction training shall also be provided to all site personnel in order to brief them on this flora of conservation interest including the locations and their importance.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-
S9.7	The resident site supervisory staff will closely monitor the conditions of concerned individuals during construction of flexible barriers in the close proximity.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Erect fences along the boundary of the works area before the commencement of works to prevent vehicle movements and encroachment of personnel onto adjacent areas.	All area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	Regularly check the work site boundaries to ensure that they are not breached and that damage does not occur to surrounding areas.	All area/ During construction	Contractor(s)/ Environmental Team (ET)		✓		Implemented	-
S9.7	Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the surrounding habitats through proper management of waste disposal.	All area/ During construction	Contractor(s)		✓		Implemented	-

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S9.7	Reinstate temporarily affected areas, particularly the habitats of plantation and shrubland-grassland immediately after completion of construction works, through on-site tree/shrub planting. The tree/shrub species will be chosen with reference to those in the surrounding area.	All area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	Affected habitats within the Clear Water Bay Country Bay shall be reinstated by hydro-seeding and planting of climbers and native shrub seedlings where practical upon completion of the slope mitigation works.	All area/ During construction	Contractor(s)		✓		N/A	-

Note: D – Design stage C – Construction O – Operation

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
<b>Landscape &amp; Visual</b>								
S11.10 & 11.11	The construction area and area allowed for temporary structures, such as the contractor's office, will be minimized to a practical minimum. (MM1)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	At the detailed design stage, the design team will seek to minimize the landscape footprint of the Project and above ground facilities, while satisfying all other requirements. (MM2)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	Design principles will be adopted to take into account the surrounding area, particularly Clear Water Bay Country Park behind and the nearby waterfront, with due consideration given to: - green roofs where practical (ie without equipment on the roof); - roadside planting; - aesthetic treatment of all structures; - vertical greening; screen planting along application site; and - landscape enhancement with amenity planting where practical including planting along the edge (site boundary) fence with native shrubs where feasible, - to reduce their visual impact and blend them into the surrounding landscape. (MM3)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	All trees within the Project Site or the potential slope mitigation works area will be carefully protected during construction according to DEVB TCW No. 10/2013 – Tree Preservation (MM4)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented, rectified after reminder	ETWB TCW No. 3/2006 - Tree Preservation.
S11.10 & 11.11	No tree within the Country Park will be felled. Trees within the Site unavoidably affected by the works will be transplanted where necessary and practical. For trees that need to be felled, compensatory planting will be provided to the satisfaction of relevant Government	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	DEVB TC(W) No. 10/2013

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	departments. A compensatory tree planting proposal including locations of tree compensation will be submitted to seek relevant government department's approval, in accordance with DEVB TC(W) No. 10/2013. (MM5)							
S11.10 & 11.11	Any slope mitigation works necessary to address natural terrain hazards, will be minimized to minimize any potential environmental impact to the Country Park e.g. soil nailing and rock stabilization will aim to avoid existing trees e.g. should any restoration of vegetation be necessary, the best planting matrix with native species will be established, with the aim of resembling the existing vegetation. (MM6)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	N/A	
S11.10 & 11.11	Dredging works for the installation of intake structures and outfall diffusers should be minimized to avoid or reduce any potential environmental impacts to as low as reasonably practicable (ALARP). The intake and outfall structures (e.g. intake openings and diffuser heads) will be prefabricated and transferred to site for installation. (MM7)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	N/A	
S11.10 & 11.11	All night-time lighting will be reduced to a practical minimum both in terms of number of level and will be hooded and directional. (MM8)units and lux level and will be hooded and directional. (MM8)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-

Note: D – Design stage C – Construction O – Operation



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
<b>Landfill Gas Hazard</b>								
S12.7	During all works, safety procedures should be implemented to minimise the risks of fires and explosions, asphyxiation of workers and toxicity effects resulting from contact with contaminated soil and groundwater.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	During trenching and excavation as well as creation of confined spaces at near to or below ground level, precautions should be clearly laid down and rigidly Gas detection equipment and appropriate breathing apparatus should be available and used when entering confined spaces or trenches deeper than 1 metre.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	The Contractor should make the workers are aware of potential hazards of working in confined spaces (any chamber, manhole or culvert which is large enough to permit access to personnel). Such work in confined spaces is controlled by the Factories and Industrial Undertakings (Confined Spaces) Regulations of the Factories and Industrial Undertakings Ordinance. Following the Safety Guide to Working in Confined Spaces ensures compliance with the above regulations.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Safety officers, specifically trained with regard to landfill gas and leachate related hazards and the appropriate actions to take in adverse circumstances, should be present on the site throughout the works, in particular, when works are undertaken below grade.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	All personnel who work on site and all visitors to the site should be made aware of the possibility of ignition of gas in the vicinity of the works, the possible presence of contaminated water and the need to avoid physical contact with it.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S12.7	Monitoring for landfill gas should be undertaken in all excavations, manholes, chambers (particularly during pipe jacking) and any confined spaces through the use of an intrinsically safe portable instrument, appropriately calibrated and capable of measuring the concentrations of methane, carbon dioxide and oxygen.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Monitoring frequency and areas to be monitored should be specified prior to commencement of groundwork, either by the Safety Officer, or by an appropriately qualified person. All measurements should be recorded and documented.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Proceed drilling with adequate care and precautions against the potential hazards which may be encountered.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Prior to the commencement of the site works, the drilling contractor should devise a 'method-of-working' statement covering all normal and emergency procedures (including but not limited to number of operatives, experience and special skills of operatives, normal method of operations, emergency procedures, supervisors responsibilities, storage and use of safety equipment, safety procedures and signs, barriers and guarding). The site supervisor and all operatives must be familiar with this statement.	All area/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Where below ground service entries are necessary to the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II), the entry point should be sealed to prevent gas entry. In addition, any below grade cable trenches entering the Incoming Switchgear Room and 132 kV Substation can become the	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	pathway for landfill gas and hence gridded metal covers should be used.							
S12.7	It is recommended regular landfill gas monitoring should be carried out at the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II). The monitoring frequency will be monthly for the first year of operation. If the monitoring results show no sign of landfill gas migration, reduce the monitoring frequency to once every six months.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	
S12.7	The manholes and utility pits within the Project Site and along the fresh water mains. Each manhole/ utility pit should be monitored with two measurements (at mid depth and base). Each measurement should be monitored for a minimum of 10 minutes. A steady reading and peak reading should be recorded at each manhole/ utility pit and for each measurement. The need for venting the manhole/ utility pit and further monitoring will be reviewed after the initial monitoring.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	All construction, operation and maintenance personnel working on-site as well as visitors should be made aware of the hazards of landfill gas and its possible presence on-site. This should be achieved through a combination of posting warning signs in prominent places and also by access to detailed information on landfill gas hazards and the designs and procedural means by which these hazards are being minimized on-site.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	

Note: D – Design stage C – Construction O – Operation

## Appendix D

# Impact Monitoring Schedule of the Reporting Month

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Jan-21						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
					1	2
3	4	5	6	7	8 Noise Impact Monitoring	9
10	11	12	13 Noise Impact Monitoring	14	15	16
17	18	19	20	21 Noise Impact Monitoring	22	23
24	25	26	27 Noise Impact Monitoring	28	29	30
31						

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

# Appendix E

## Noise Monitoring Equipment Calibration Certificate

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



**綜合試驗有限公司**  
**SOILS & MATERIALS ENGINEERING CO., LTD.**  
 香港新界葵涌永基路22-24號椰林閣集團大廈全幢  
 The Whole Block of YLK Group Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong.  
 Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com



**CERTIFICATE OF CALIBRATION**

Certificate No.: 20CA0803 01 Page: 1 of 2

**Item tested**

Description: Acoustical Calibrator (Class 1)  
 Manufacturer: Pulsar Instruments Ltd.  
 Type/Model No.: 105  
 Serial/Equipment No.: 63705  
 Adaptors used: -

**Item submitted by**

Customer: Acuity Sustainability Consulting Limited.  
 Address of Customer: -  
 Request No.: -  
 Date of receipt: 03-Aug-2020

**Date of test:** 06-Aug-2020

**Reference equipment used in the calibration**

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2341427	11-May-2021	SCL
Preamplifier	B&K 2673	2743150	03-Jun-2021	CEPREI
Measuring amplifier	B&K 2610	2346941	03-Jun-2021	CEPREI
Signal generator	DS 360	33873	19-May-2021	CEPREI
Digital multi-meter	34401A	US36087050	19-May-2021	CEPREI
Audio analyzer	8903B	GB4.1300350	18-May-2021	CEPREI
Universal counter	53132A	MY40003662	18-May-2021	CEPREI

**Ambient conditions**

Temperature: 22 ± 1 °C  
 Relative humidity: 55 ± 10 %  
 Air pressure: 1005 ± 5 hPa



**Test specifications**

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

**Test results**

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.

Approved Signatory:  Date: 07-Aug-2020 Company Chop: 

**Comments:** The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

HKAS has accredited this laboratory (Reg. No. HOKLAS 028) under HOKLAS for specific calibration activities as listed in the HOKLAS directory of accredited laboratories. The results shown in this certificate are traceable to the International System of Units (SI) or recognised measurement standards. The results relate only to the item(s) calibrated. This certificate shall not be reproduced except in full without approval of the laboratory.







## Certificate of Calibration

for

Description: Sound Level Meter  
Manufacturer: NTi Audio  
Type No.: XL2 (Serial No.: A2A-13548-E0)  
Microphone: ACO 7052 (Serial No.:73780)  
Preamplifier: NTi Audio MA220 (Serial No.:5235)

Submitted by:

Customer: Acuity Sustainability Consulting Limited  
Address: Unit 1908, iPlace, Nos. 301-305 Castle Peak Road,  
Kwai Chung, New Territories

Upon receipt for calibration, the instrument was found to be:

- Within  
 Outside

the allowable tolerance.

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 6 January 2020

Date of calibration: 10 January 2020

Calibrated by:   
Calibration Technician

Certified by:   
Tang Cheuk Hang  
Quality Manager

Date of issue: 10 January 2020

Certificate No.: APJ19-143-CC001



Page 1 of 4



**1. Calibration Precaution:**

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

**2. Calibration Conditions:**

Air Temperature: 23.0 °C  
 Air Pressure: 1006 hPa  
 Relative Humidity: 71.0 %

**3. Calibration Equipment:**

	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV180064	HOKLAS

**4. Calibration Results**

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	1000	94.0	+0.4

Linearity

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	1000	94.0	Ref
				104		104.0	±0.3
				114		114.0	±0.3

Time Weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	1000	94.0	Ref
			Slow			94.0	±0.3

Certificate No.: APJ19-143-CC001



Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong  
 Tel: (852) 2668 3423 Fax: (852) 2668 6946  
 Homepage: <http://www.aa-lab.com> E-mail: [inquirv@aa-lab.com](mailto:inquirv@aa-lab.com)



Frequency Response

Linear Response

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dB	SPL	Fast	94	31.5	94.0	±2.0
					63	94.1	±1.5
					125	94.1	±1.5
					250	94.0	±1.4
					500	94.0	±1.4
					1000	94.0	Ref
					2000	93.8	±1.6
					4000	93.4	±1.6
					8000	92.4	+2.1; -3.1

A-weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	31.5	54.8	-39.4±2.0
					63	67.9	-26.2±1.5
					125	78.0	-16.1±1.5
					250	85.4	-8.6±1.4
					500	90.8	-3.2±1.4
					1000	94.0	Ref
					2000	95.0	+1.2±1.6
					4000	94.4	+1.0±1.6
					8000	91.3	-1.1±2.1; -3.1

C-weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBC	SPL	Fast	94	31.5	91.0	-3.0±2.0
					63	93.3	-0.8±1.5
					125	93.9	-0.2±1.5
					250	94.1	-0.0±1.4
					500	94.1	-0.0±1.4
					1000	94.0	Ref
					2000	93.6	-0.2±1.6
					4000	92.6	-0.8±1.6
					8000	89.4	-3.0±2.1; -3.1

Certificate No.: APJ19-143-CC001



Page 3 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong  
 Tel: (852) 2668 3423 Fax: (852) 2668 6946  
 Homepage: <http://www.aa-lab.com> E-mail: [inquirv@aa-lab.com](mailto:inquirv@aa-lab.com)



**5. Calibration Results Applied**

The results apply to the particular unit-under-test only. All calibration points are within manufacture's specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.10
	63 Hz	± 0.05
	125 Hz	± 0.10
	250 Hz	± 0.10
	500 Hz	± 0.10
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	± 0.05
	8000 Hz	± 0.10
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

**Note:**

The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)\*L shall not be liable for any loss or damage resulting from the use of the equipment.



Certificate No.: APJ19-143-CC001

Page 4 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong  
 Tel: (852) 2668 3423 Fax: (852) 2668 6946  
 Homepage: <http://www.aa-lab.com> E-mail: [inquirv@aa-lab.com](mailto:inquirv@aa-lab.com)



## Certificate of Calibration

for

Description: *Sound Level Meter*  
Manufacturer: *NTi Audio*  
Type No.: *XL2 (Serial No.: A2A-13663-E0)*  
Microphone: *ACO 7052 (Serial No.: 73912)*  
Preamplifier: *NTi Audio MA220 (Serial No.: 5735)*

Submitted by:

Customer: *Acuity Sustainability Consulting Limited*  
Address: *Unit C, 11/F, Ford Giory Plaza, No. 37-39 Wing Hong Street,  
Cheung Sha Wan, Kowloon, Hong Kong*

Upon receipt for calibration, the instrument was found to be:

- Within  
 Outside


the allowable tolerance.

The test equipment used for calibration are traceable to National Standards via:  
- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: *08 September 2020*

Date of calibration: *09 September 2020*

Calibrated by:   
Calibration Technician

Certified by:   
Mr. Ng Yan Wa  
Laboratory Manager

Date of issue: *09 September 2020*

Certificate No.: *AP120-104-CC001*



Page 1 of 4



**1. Calibration Precaution:**

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

**2. Calibration Conditions:**

Air Temperature: 23.8°C  
 Air Pressure: 1008 hPa  
 Relative Humidity: 62.5%

**3. Calibration Equipment:**

	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2388467	AV200041	HOKLAS

**4. Calibration Results**

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)				Applied value		UUT Reading	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	1000	94.0	±0.4

Linearity

Setting of Unit-under-test (UUT)				Applied value		UUT Reading	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	1000	94.0	Ref
				104		104.0	±0.3
				114		114.0	±0.3

Time Weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	Fast	94	1000	94.0	Ref
			Slow			94.0	±0.3

Certificate No.: APJ20-104-CU001



Page 2 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Sha Tin, N.T., Hong Kong  
 Tel: (852) 2668 3423 Fax: (852) 2668 6946  
 Homepage: <http://www.aat-lab.com> E-mail: [info@aat-lab.com](mailto:info@aat-lab.com)



Frequency Response

Linear Response

Setting of Unit-under-test (UUT)				Applied value		UUT Reading	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dB	SPL	94	31.5	94.2	±2.0	
				63	94.3	±1.5	
				125	94.3	±1.5	
				250	94.2	+1.4	
				500	94.1	+1.4	
				1000	94.0	Ref	
				2000	93.8	±1.6	
				4000	93.6	±1.6	
			8000	93.4	-2.1; -3.1		

A-weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dBA	SPL	94	31.5	54.8	-39.4 ±2.0	
				63	68.0	-26.2 ±1.5	
				125	78.1	-16.1 ±1.5	
				250	85.5	-8.6 ±1.4	
				500	90.8	-3.2 ±1.4	
				1000	94.0	Ref	
				2000	95.0	+1.2 ±1.6	
				4000	94.6	+1.0 ±1.6	
			8000	92.3	-1.1 ±2.1; -3.1		

C-weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
30-130	dB	SPL	94	31.5	91.2	-3.0 ±2.0	
				63	93.4	-0.8 ±1.5	
				125	94.1	-0.2 ±1.5	
				250	94.1	-0.0 ±1.4	
				500	94.1	-0.0 ±1.4	
				1000	94.0	Ref	
				2000	93.6	-0.2 ±1.6	
				4000	92.8	-0.8 ±1.6	
			8000	90.4	-3.0 ±2.1; -5.1		

Certificate No.: APJ20-104-CC001



Page 3 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong  
Tel: (852) 2668 3423 Fax: (852) 2668 6946  
Homepage: <http://www.aat-lab.com> E-mail: [inquiry@aat-lab.com](mailto:inquiry@aat-lab.com)



**5. Calibration Results Applied**

The results apply to the particular unit-under-test only. All calibration points are within manufacturer's specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 cB	31.5 Hz	± 0.05
	63 Hz	± 0.05
	125 Hz	± 0.05
	250 Hz	± 0.05
	500 Hz	+ 0.05
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	+ 0.05
104 dB	1000 Hz	± 0.05
	2000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

**Note:**

The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)\*L shall not be liable for any loss or damage resulting from the use of the equipment.

Certificate No.: APJ20-104-CC001



Page 4 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong  
 Tel: (852) 2668 5423 Fax: (852) 2668 6946





## Certificate of Calibration

for

Description: Sound Level Meter  
Manufacturer: SVANTEK  
Type No.: 971 (Serial No.: 77731)  
Microphone: ACO 7052E (Serial No.: 72681)  
Preamplifier: SV18 (Serial No.: 78763)

### Submitted by:

Customer: Acuity Sustainability Consulting Limited  
Address: Unit C, 11/F., Ford Glory Plaza, No. 37-39 Wing Hong  
Street, Cheung Sha Wan, Kowloon

Upon receipt for calibration, the instrument was found to be:

- Within  
 Outside

the allowable tolerance.

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory

Date of receipt: 12 February 2020

Date of calibration: 13 February 2020

Calibrated by:   
Calibration Technician

Certified by:   
Mr. Ng Yan Wa  
Laboratory Manager

Date of issue: 13 February 2020

Certificate No.: APJ19-160-CC001



Page 1 of 4



**1. Calibration Precaution:**

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.

**2. Calibration Conditions:**

Air Temperature: 23.7°C  
 Air Pressure: 1006 hPa  
 Relative Humidity: 66.2 %

**3. Calibration Equipment:**

	Type	Serial No.	Calibration Report Number	Traceable to
Multifunction Calibrator	B&K 4226	2288467	AV180064	HOKLAS

**4. Calibration Results**

Sound Pressure Level

Reference Sound Pressure Level

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
34.2-136.2	dBA	SPL	Fast	94	1000	94.0	±0.4

Linearity

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
34.2-136.2	dBA	SPL	Fast	1000	94	94.0	Ref
					104	104.0	±0.3
					114	114.0	±0.3

Time Weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading,	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
34.2-136.2	dBA	SPL	94	1000	Fast	94.0	Ref
					Slow	94.0	±0.3

Certificate No.: APJ19-160-CC001



Page 2 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong  
 Tel: (852) 2668 3423 Fax: (852) 2668 6946  
 Homepage: <http://www.aa-lab.com> E-mail: [inquirv@aa-lab.com](mailto:inquirv@aa-lab.com)



Frequency Response

Linear Response

Setting of Unit-under-test (UUT)				Applied value		UUT Reading	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
34.2-136.2	dB	SPL	Fast	94	31.5	94.1	±2.0
					63	94.0	±1.5
					125	93.9	±1.5
					250	93.9	±1.4
					500	93.9	±1.4
					1000	94.0	Ref
					2000	94.1	±1.6
					4000	93.9	±1.6
				8000	91.2	+2.1; -3.1	

A-weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
34.2-136.2	dBA	SPL	Fast	94	31.5	54.8	-39.4±2.0
					63	67.8	-26.2±1.5
					125	77.9	-16.1±1.5
					250	85.3	-8.6±1.4
					500	90.7	-3.2±1.4
					1000	94.0	Ref
					2000	95.3	+1.2±1.6
					4000	94.9	+1.0±1.6
				8000	90.1	-1.1±2.1; -3.1	

C-weighting

Setting of Unit-under-test (UUT)				Applied value		UUT Reading	IEC 61672 Class 1
Range, dB	Freq. Weighting	Time Weighting	Level, dB	Frequency, Hz	dB	Specification, dB	
34.2-136.2	dBC	SPL	Fast	94	31.5	91.1	-3.0±2.0
					63	93.2	-0.8±1.5
					125	93.7	-0.2±1.5
					250	93.9	-0.0±1.4
					500	93.9	-0.0±1.4
					1000	94.0	Ref
					2000	93.8	-0.2±1.6
					4000	93.1	-0.8±1.6
				8000	88.2	-3.0±2.1; -3.1	



Certificate No.: APJ19-160-CC001

Page 3 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong  
 Tel: (852) 2668 3423 Fax: (852) 2668 6946  
 Homepage: <http://www.aa-lab.com> E-mail: [inquirv@aa-lab.com](mailto:inquirv@aa-lab.com)



**5. Calibration Results Applied**

The results apply to the particular unit-under-test only. All calibration points are within manufacture’s specification as IEC 61672 Class 1.

Uncertainties of Applied Value:

94 dB	31.5 Hz	± 0.15
	63 Hz	± 0.10
	125 Hz	± 0.10
	250 Hz	± 0.10
	500 Hz	± 0.10
	1000 Hz	± 0.05
	2000 Hz	± 0.05
	4000 Hz	± 0.05
	8000 Hz	± 0.15
104 dB	1000 Hz	± 0.05
114 dB	1000 Hz	± 0.05

The uncertainties are evaluated for a 95% confidence level.

Note:


The values given in this certification only related to the values measured at the time of the calibration and any uncertainties quoted will not allow for the equipment long-term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the calibration. (A+A)\*L shall not be liable for any loss or damage resulting from the use of the equipment.




Certificate No.: APJ19-160-CC001

Page 4 of 4

Room 422, Leader Industrial Centre, 57-59 Au Pui Wan Street, Fo Tan, Shatin, N.T., Hong Kong  
 Tel: (852) 2668 3423 Fax: (852) 2668 6946  
 Homepage: <http://www.aa-lab.com> E-mail: [inquirv@aa-lab.com](mailto:inquirv@aa-lab.com)





This instrument was produced under rigorous factory production control and documented standard procedures. It was individually visually inspected, leak tested and function tested for display, backlight, button and software performance. The accuracy of each of its primary measurements was individually calibrated and/or tested against standards traceable to the National Institute of Standards and Technology ("NIST") or calibrated intermediary standards. This instrument is certified to have performed at the time of manufacture in compliance with the following specifications as they apply to this meter's specific model, measurements and features.

### Methods Used in Calibration and Testing

#### Wind Speed:

The Kestrel Weather & Environmental Meter impeller installed in this unit was individually tested in a subsonic wind tunnel operating at approximately 300 fpm (1.5 m/s) and 1200 fpm (6.1 m/s) monitored by a Gill Instruments Model 1350 ultrasonic time-of-flight anemometer. The Standard's maximum combined uncertainty is  $\pm 1.04\%$  within the airspeed range 706.6 to 3923.9 fpm (3.59 to 19.93 m/s), and  $\pm 1.66\%$  within the airspeed range 166.6 to 706.6 fpm (0.85 to 3.59 m/s).

#### Temperature:

Temperature response is verified in comparison with a Eutechnics 4600 Precision Thermometer or a standard Kestrel 4000 Weather & Environmental Meter calibrated weekly against the Eutechnics 4600. The Eutechnics 4600 is calibrated annually and is traceable to NIST with a system accuracy of  $\pm 0.05^\circ\text{C}$ .

#### Direction / Heading

The sensitivity of the magnetic directional sensor is verified at the component level by applying a magnetic field to the sensor and measuring the signal output at 4 points, as well as after assembly by orienting the unit to the cardinal directions and measuring the magnetic field output. In both cases, the compass output must be accurate to within  $\pm 5$  degrees.


#### Relative Humidity:

Relative humidity receives a two-point calibration in humidity and temperature controlled chambers at 75.3% RH and 32.8% RH at  $25^\circ\text{C}$ . The calibration tanks are monitored with an Edgetech Model 2002 DewPrime II Standard Chilled Mirror Hygrometer. Following calibration, performance is further verified at an RH of approximately 43.2% against the Edgetech Hygrometer. The Edgetech Hygrometer is calibrated annually and is traceable to NIST with a maximum relative expanded uncertainty of  $\pm 0.2\%$  RH.

#### Barometric Pressure:

Pressure response is verified against a Vaisala PTB210A Digital Barometer or a standard Kestrel 4000 Weather & Environmental Meter calibrated weekly against the Vaisala Barometer. The Vaisala Barometer is calibrated annually and is traceable to NIST with an accuracy of  $\pm 0.15\text{ hPa}$  at  $\pm 20^\circ\text{C}$  defined as the root sum of the squares (RSS) of end point non-linearity, hysteresis error, repeatability error and calibration uncertainty at room temperature.

**Approved By:**



Michael Naughton, Engineering Manager

The enclosed Kestrel Weather & Environmental Meter was manufactured by Nissen-Kellerman Co. at its facilities located at 21 Creek Circle, Boothwyn, PA 19061 USA.



# Appendix F

## Event/Action Plan for Noise Exceedance

**Event and Action Plan for Construction Noise Monitoring**

Event	Action	ET	IEC	ER	Contractor
Action Level	<ol style="list-style-type: none"> <li>Carry out investigation to identify the source and cause of the complaint/ exceedance(s)</li> <li>Notify IEC, ER, and Contractor and report the results of investigation to the Contractor, ER and the IEC</li> <li>Discuss with the Contractor and IEC for remedial measures required</li> <li>If the complaint is related to the Project, conduct additional monitoring for checking mitigation effectiveness and report the findings and results to the IEC, ER and the Contractor</li> </ol>	<ol style="list-style-type: none"> <li>Review the analyzed results submitted by the ET</li> <li>Review the proposed remedial measures by the Contractor and advise the ER accordingly</li> <li>Supervise the implementation of remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>Confirm receipt of Notification of Exceedance in writing</li> <li>Require Contractor to propose remedial measures for the analysed noise problem</li> <li>Ensure remedial measures are properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>Submit noise mitigation proposals, if required, to the IEC and ER</li> <li>Implement noise mitigation proposals.</li> </ol>	

Limit Level	<ol style="list-style-type: none"> <li>Notify IEC, ER, EPD and Contractor</li> <li>Identify the source(s) of impact by reviewing all the relevant monitoring data and the corresponding construction activities. Exceedances should also be confirmed by immediate verification in the field as far as practical.</li> <li>Repeat measurement to confirm findings</li> <li>Increase monitoring frequency</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>inform IEC, ER and EPD the cause &amp; actions taken for the exceedances</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results</li> <li>If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions</li> <li>Review Contractor's remedial actions to assure their effectiveness and advise the ER &amp; ET accordingly</li> <li>Supervise the implementation of the remedial measures</li> </ol>	<ol style="list-style-type: none"> <li>Confirm receipt of notification of exceedance in writing</li> <li>Notify Contractor</li> <li>Require Contractor to propose remedial measures for the analyzed noise problem</li> <li>Ensure remedial measures are properly implemented</li> <li>If exceedance continuous, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is aborted</li> </ol>	<ol style="list-style-type: none"> <li>Take immediate action to avoid further exceedance</li> <li>Identify practicable measures to minimize the noise impact. Submit proposals for remedial actions to ER within three working days of notification</li> <li>Implement the agreed proposals</li> <li>Resubmit proposal if problem still not under control</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated</li> </ol>
-------------	---	--	---	---



# Appendix G

## Noise Monitoring Data

Date	Time	Weather	Leq-5min, dB(A)						Leq-30min, dB(A)	Leq30 (min) L <sub>10</sub> dB(A)	Leq30 (min) L <sub>90</sub> dB(A)	Limit Level, dB(A)
			Reading (1)	Reading (2)	Reading (3)	Reading (4)	Reading (5)	Reading (6)				
08/01/2021	16:05 - 16:35	cloudy	67.3	68.8	69.0	68.8	68.8	67.2	68.4	71.8	60.2	70.0
13/01/2021	13:10 - 13:40	sunny	67.4	67.5	69.5	67.6	67.3	67.3	67.8	71.4	57.8	70.0
21/01/2021	11:37 - 12:07	sunny	65.4	67.3	66.9	67.9	65.8	66.8	66.8	70.1	57.6	70.0
27/01/2021	12:40 - 13:10	sunny	61.6	69.5	65.6	64.1	68.1	69.7	67.3	70.0	59.9	70.0

Remarks: The Education Bureau (EDB) has announced that all kindergartens as well as primary and secondary schools (including special schools and schools offering non-local curriculum) will continue to suspend face to face classes and school activities until the beginning of school's Chinese New Year holidays due to the spread of the Novel Coronavirus. Further information and Academic School Calendar can be found in Appendix O.

# Appendix H

## Waste Flow Table

**Monthly Summary Waste Flow Table**

**Name of Department: WSD Contract No. / Works Order No.: 13/WSD/16**

**Monthly Summary Waste Flow Table for January 2021**

Month	Actual Quantities of <u>Inert</u> Construction Waste Generated Monthly					
	Total Quantity Generated (see Note 4)	Hard Rock and Large Broken Concrete (see Note 3)	Reused in the Contract	Reused in other Projects	Disposed of as Public Fill	Imported Fill (see Note 1)
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )
2018	1.157	0.063	0.000	0.000	1.157	0.518
2019	5.178	0.043	2.211	0.000	2.520	3.200
2020	13.173	1.506	0.291	0.000	12.878	1.323
Jan 2021	2.438	0.120	0.000	0.000	2.438	0.127
<b>Total for 2021</b>	<b>2.438</b>	<b>0.120</b>	<b>0.000</b>	<b>0.000</b>	<b>2.438</b>	<b>0.127</b>

**Contract No. 13/WSD/16  
Mainlaying in Tseung Kwan O  
Monthly EM&A Report No.30**



Month	Actual Quantities of <u>Non-inert</u> Construction Waste Generated Monthly				
	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. General Refuse disposed at Landfill
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )
2018	0.000	0.417	0.000	0.000	0.139
2019	0.000	0.062	0.000	0.000	0.102
2020	0.000	0.606	0.000	0.000	0.043
Jan 2021	0.000	0.065	0.000	0.000	0.006
<b>Total for 2021</b>	<b>0.000</b>	<b>0.065</b>	<b>0.000</b>	<b>0.000</b>	<b>0.006</b>

- Notes:
1. The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  2. Plastic refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
  3. Broken concrete for recycling into aggregate.

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



4. “Total Quantity Generated” only refers to the actual quantities of inert C&D materials generated monthly excluding those that will be recycled (Hard Rock and Large Broken Concrete, Reused in the Contract, Reused in other Projects). Imported fill will not be included in “Total Quantity Generated” as those C&D materials are not generated from this project.
5. C&D materials in tonnes are converted to meter cube (m<sup>3</sup>) on a scale of 0.5.
6. Source and types of Imported Fill in the reporting month
  - i. K. Wah Quarry Company Limited: (Soil) 127.22m<sup>3</sup> (254.44 tonnes/10 cars)

7. The amount of Hard Rock and Large Broken Concrete are disposed to public fill, the breakdown of C&D materials disposed to public fill is shown as below:

Type of C&D Materials	Description of C&D Materials	C&D Waste Disposed (Volume) (m <sup>3</sup> )
Inert	Bentonite	--
	Broken Concrete	53.95
	Broken Rock	191.2
	Mixed Construction Waste (>50% inert)	--
	Building Debris	5.20
	Mixed Rock and Soil	1346.7
	Reclaimed Asphalt Pavement	294.15
	Slurry	314.25
	Soil	232.95
	<b>TOTAL =</b>	<b>2834.4</b>
Non-inert	<b>TOTAL =</b>	<b>5.5</b>

# Appendix I

**Landfill  
Equipment  
Certificate**

**Gas**

**Monitoring  
Calibration**



香港新界葵涌葵昌路58-70號永祥工業大廈10樓B室  
 Unit B, 10/F., Wing Cheung Industrial Building, 58-70 Kwai Cheong Road, Kwai Chung, New Territories, HK  
 Tel: (852) 2751 7770 Fax: (852) 2756 2051 E-mail: rotter@rotter.com.hk

**Calibration Report - Gas Detector**

**PGM-2500 (QRAE III) --- LEL/O2/CO/H2S**

**UNIT INFORMATION :**

Customer:	Penta Ocean Construction Co Ltd	Serial # :	M02A016735	Model :	QRAE III
		Firmware :	V2.14	Sensor :	LEL/O2/CO/H2S
		Cal date :	28-Jul-2020	Inspected:	Teddy

**SENSOR DATA :**

	LEL sensor (ME)	O2 sensor	CO sensor (Tox1)	H2S sensor (Tox2)
Calibration dates:	28-Jul-2020	28-Jul-2020	28-Jul-2020	28-Jul-2020
After Calibration levels	50%	18.00%	50 ppm	10.1 ppm
Alarm levels (Low):	10.00%	19.50%	35 ppm	10 ppm
Alarm levels (High):	20.00%	23.50%	200 ppm	20 ppm
TWA Level :	--	--	35 ppm	10 ppm
STEL Level :	--	--	100 ppm	15 ppm

**Status:**

Pump Speed	Low	Back Light	Manual
Clock	Yes	Measure	Average

**LEL Gas Selection**

LEL Calibration Gas	Methane	LEL measurement Gas	Methane
LEL Custom Gas	LEL_custom_gas	LEL Custom Factor	1.0

Gas types used : 4-Gas Mix: (18% O2, 50ppm CO, 10ppm H2S, 50% LEL CH4, BAL N2) Gas lot #13333090 Cyl# 18  
 \*\*\* Fresh Air Calibration is highly recommended to proceed prior for measurement each time.

Replaced Parts:

**Notes:**

The unit was calibrated and checked under good working condition

\*\*Next calibration date on or before 27 July 2021

Serviced by  Teddy Wong  
 Rotter International Ltd



# Appendix J

## Landfill Gas Monitoring Data

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	2-1-2021	0830	Fine	0	0	0	20.9	11/1025	4.2
	2-1-2021	1930	Fine	0	0	0	20.9	18/1021	4.2
	2-1-2021	1700	Fine	0	0	0	20.2	15/1020	4.2
Area B	2-1-2021	0849	Fine	0	0	0	20.9	11/1025	2.5
	2-1-2021	1347	Fine	0	0	0	20.9	18/1021	2.5
	2-1-2021	1647	Fine	0	0	0	20.9	15/1020	2.5

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		2-1-2021
Laboratory Staff:			
Checked by:			2-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.FC 4A0	2/1/2021	0835	Fine	0	0	0	20.9	12 / 1025	2.5
	2/1/2021	1355	Fine	0	0	0	20.9	16 / 1021	2.5
CH.FC 040	2/1/2021	0900	Fine	0	0	0	20.9	12 / 1025	2.5
	2/1/2021	1400	Fine	0	0	0	20.9	16 / 1021	2.5
P.F.C	2/1/2021	0915	Fine	0	0	0	20.9	12 / 1025	2
	2/1/2021	1415	Fine	0	0	0	20.9	16 / 1021	2
137CHCT 2+66	2/1/2021	0935	Fine	0	0	0	20.9	13 / 1025	3.1
	2/1/2021	1435	Fine	0	0	0	20.9	16 / 1021	3.1
137 P.F.C	2/1/2021	0945	Fine	0	0	0	20.9	13 / 1025	1.4
	2/1/2021	1445	Fine	0	0	0	20.9	16 / 1021	1.4
137 P.F.B	2/1/2021	0955	Fine	0	0	0	20.9	13 / 1025	6.2
	2/1/2021	1455	Fine	0	0	0	20.9	16 / 1021	6.2
137 P.F.A	2/1/2021	1005	Fine	0	0	0	20.9	14 / 1025	6.2
	2/1/2021	1305	Fine	0	0	0	20.9	16 / 1021	6.2

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		2/1/2021
Laboratory Staff:			
Checked by:			

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated:
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPE 1	2/1/2021	1015	Fine	0	0	0	20.9	14/1024	2.2
	2/1/2021	1015	Fine	0	0	0	20.9	18/1021	2.2
Pit A	2/1/2021	1045	Fine	0	0	0	20.9	13/1024	3
	2/1/2021	1045	Fine	0	0	0	20.9	16/1021	3
Pit B	2/1/2021	1055	Fine	0	0	0	20.9	15/1024	8
	2/1/2021	1055	Fine	0	0	0	20.9	16/1021	8
								/	
								/	
								/	
								/	
								/	
								/	
								/	

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RenoPipe])                                           2/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
FGM-2500 (QRAEIII)	29 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	4-1-2021	0837	Fine	0	0	0	20.9	17 / 1023	4.2
	4-1-2021	1338	Fine	0	0	0	20.9	20 / 1020	4.2
	4-1-2021	1709	Fine	0	0	0	20.9	19 / 1020	4.2
Area B	4-1-2021	0848	Fine	0	0	0	20.9	17 / 1023	2.5
	4-1-2021	1348	Fine	0	0	0	20.9	20 / 1020	2.5
	4-1-2021	1648	Fine	0	0	0	20.9	19 / 1020	2.5

Name & Designation      Signature      Date

Field Operator:      Eric Man (Sub-Agent [RenoPipe])           4-1-2021

Laboratory Staff:

Checked by:      W. C. Leung (Assistant Foreman)           4-1-2021

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 410	4/1/2021	0835	Fine	0	0	0	20.9	17/1023	2.5
	4/1/2021	1335	Fine	0	0	0	20.9	20/1022	2.5
CHFC 046	4/1/2021	0900	Fine	0	0	0	20.9	17/1023	2.5
	4/1/2021	1400	Fine	0	0	0	20.9	20/1019	2.5
P1C	4/1/2021	0915	Fine	0	0	0	20.8	17/1023	2
	4/1/2021	1415	Fine	0	0	0	20.6	20/1019	2
131 CHFC2+6	4/1/2021	0935	Fine	0	0	0	20.9	17/1023	3.1
	4/1/2021	1435	Fine	0	0	0	20.6	20/1019	3.1
131 P1C	4/1/2021	0945	Fine	0	0	0	20.9	17/1023	1.4
	4/1/2021	1445	Fine	0	0	0	20.9	20/1019	1.4
131 P1B	4/1/2021	0955	Fine	0	0	0	20.9	18/1023	6.2
	4/1/2021	1455	Fine	0	0	0	20.9	20/1019	6.2
131 P1A	4/1/2021	1005	Fine	0	0	0	20.9	18/1023	6.2
	4/1/2021	1505	Fine	0	0	0	20.9	20/1019	6.2

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		4/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	25 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WR1	4/1/2021	1015	Fine	0	0	0	20.9	18/1023	2.2
	4/1/2021	1515	Fine	0	0	0	20.9	20/1019	2.2
PA	4/1/2021	1245	Fine	0	0	0	20.9	18/1027	3
	4/1/2021	1500	Fine	0	0	0	20.9	20/1019	3
PB	4/1/2021	1035	Fine	0	0	0	20.9	18/1023	3
	4/1/2021	1535	Fine	0	0	0	20.9	20/1019	3
								/	
								/	
								/	
								/	
								/	
								/	
								/	

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           4/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PCM-2500 (QRAEIII)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	5-1-2021	0830	Fine	0	0	0	20.9	18 / 1022	4.2
	5-1-2021	1330	Fine	0	0	0	20.9	22 / 1019	4.2
	5-1-2021	1700	Fine	0	0	0	20.9	20 / 1019	4.2
Area B	5-1-2021	0845	Fine	0	0	0	20.9	18 / 1022	2.5
	5-1-2021	1345	Fine	0	0	0	20.9	22 / 1019	2.5
	5-1-2021	1645	Fine	0	0	0	20.9	20 / 1019	2.5

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		5-1-2021
Laboratory Staff:			
Checked by:	W.C. Leung (Assistant Foreman)		5-1-2021



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4730	5/1/2021	0835	Fine	0	0	0	20.4	18/1022	2.5
	5/1/2021	1535	Fine	0	0	0	20.4	22/1018	2.5
CHFC 0790	5/1/2021	0910	Fine	0	0	0	20.4	18/1022	2.5
	5/1/2021	1440	Fine	0	0	0	20.4	22/1018	2.5
Pit C	5/1/2021	0918	Fine	0	0	0	20.4	18/1022	2
	5/1/2021	1415	Fine	0	0	0	20.4	22/1018	2
141 PTC 2460	5/1/2021	0935	Fine	0	0	0	20.4	18/1022	2.1
	5/1/2021	1435	Fine	0	0	0	20.4	22/1018	2.1
141 PTC	5/1/2021	0945	Fine	0	0	0	20.4	18/1022	1.4
	5/1/2021	1445	Fine	0	0	0	20.4	22/1018	1.4
141 PTC	5/1/2021	0955	Fine	0	0	0	20.4	18/1022	6.2
	5/1/2021	1455	Fine	0	0	0	20.4	22/1018	6.2
141 PTA	5/1/2021	1005	Fine	0	0	0	20.4	19/1022	6.2
	5/1/2021	1505	Fine	0	0	0	20.4	22/1018	6.2

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		5/1/2021
Laboratory Staff:			
Checked by:			

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPE1	5/1/2021	1015	Fine	0	0	0	20.9	19/1022	2.2
	5/1/2021	1515	Fine	0	0	0	20.9	21/1018	2.2
P1A	5/1/2021	1041	Fine	0	0	0	20.9	19/1021	3
	5/1/2021	1545	Fine	0	0	0	20.9	21/1018	3
P1B	5/1/2021	1055	Fine	0	0	0	20.9	19/1021	8
	5/1/2021	1555	Fine	0	0	0	20.9	21/1018	8
								/	
								/	
								/	
								/	
								/	
								/	
								/	

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           5/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAEIII)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	6-1-2021	0830	Fine	0	0	0	20.9	15/1022	4.2
	6-1-2021	1330	Fine	0	0	0	20.9	19/1017	4.2
	6-1-2021	1730	Fine	0	0	0	20.9	17/1018	4.2
Area B	6-1-2021	0845	Fine	0	0	0	20.9	15/1022	2.5
	6-1-2021	1345	Fine	0	0	0	20.9	19/1017	2.5
	6-1-2021	1645	Fine	0	0	0	20.9	17/1018	2.5

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		6-1-2021
Laboratory Staff:			
Checked by:	W.C. Leung (Assistant Person)		6-1-2021

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.Fc 4+50	6/1/2021	0835	Fine	0	0	0	20.9	16 / 1022	2.5
	6/1/2021	1355	Fine	0	0	0	20.9	19 / 1017	2.5
CH.Fc 0+40	6/1/2021	0900	Fine	0	0	0	22.9	16 / 1022	2.5
	6/1/2021	1400	Fine	0	0	0	22.9	19 / 1017	2.5
P+ C	6/1/2021	0915	Fine	0	0	0	20.9	16 / 1022	8
	6/1/2021	1415	Fine	0	0	0	20.9	19 / 1017	8
147(CHC) 2+60	6/1/2021	0935	Fine	0	0	0	20.9	16 / 1022	2.1
	6/1/2021	1435	Fine	0	0	0	22.9	19 / 1017	2.1
147 P+ C	6/1/2021	0945	Fine	0	0	0	20.9	16 / 1022	1.4
	6/1/2021	1445	Fine	0	0	0	22.9	19 / 1017	1.4
147 P+ E	6/1/2021	0955	Fine	0	0	0	22.9	16 / 1022	6.2
	6/1/2021	1455	Fine	0	0	0	22.9	19 / 1017	6.2
147 P+ A	6/1/2021	1005	Fine	0	0	0	20.9	16 / 1022	6.2
	6/1/2021	1505	Fine	0	0	0	22.9	19 / 1017	6.2

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RencPipe])                                            6/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR1	6/1/2021	1035	Fine	0	0	0	20.9	16 / 1022	2.2
	6/1/2021	1315	Fine	0	0	0	20.9	18 / 1017	2.2
RTA	6/1/2021	1045	Fine	0	0	0	20.9	16 / 1021	3
	6/1/2021	1345	Fine	0	0	0	20.9	18 / 1017	3
RTB	6/1/2021	1055	Fine	0	0	0	20.9	16 / 1021	3
	6/1/2021	1355	Fine	0	0	0	20.9	18 / 1017	3

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RanoPipe])                      *TW*                      6/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAEIII)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	7-1-2021	0830	Fine	0	0	0	20.9	14 / 1022	4.2
	7-1-2021	1330	Fine	0	0	0	20.9	17 / 1019	4.2
	7-1-2021	1700	Fine	0	0	0	20.9	18 / 1020	4.2
Area B	7-1-2021	0845	Fine	0	0	0	20.9	14 / 1022	2.5
	7-1-2021	1345	Fine	0	0	0	20.9	17 / 1019	2.5
	7-1-2021	1645	Fine	0	0	0	20.9	15 / 1023	2.5

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		7-1-2021
Laboratory Staff:			
Checked by:			7-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 450	7/1/2021	0838	Fine	0	0	0	20.4	14/1022	2.5
	7/1/2021	1333	Fine	0	0	0	20.4	17/1019	2.5
CHFC 240	7/1/2021	0900	Fine	0	0	0	20.4	14/1022	2.7
	7/1/2021	1400	Fine	0	0	0	20.4	17/1019	2.7
P+C	7/1/2021	0915	Fine	0	0	0	20.4	14/1022	3
	7/1/2021	1415	Fine	0	0	0	20.4	17/1019	3
197 CHFC 2466	7/1/2021	0935	Fine	0	0	0	20.4	14/1022	3.1
	7/1/2021	1437	Fine	0	0	0	20.4	17/1019	3.1
197 P+C	7/1/2021	0947	Fine	0	0	0	20.4	14/1022	1.4
	7/1/2021	1447	Fine	0	0	0	20.4	17/1019	1.4
197 V.F.B	7/1/2021	0955	Fine	0	0	0	20.4	14/1022	6.2
	7/1/2021	1455	Fine	0	0	0	20.4	16/1019	6.2
197 V.F.A	7/1/2021	1005	Fine	0	0	0	20.4	15/1022	6.2
	7/1/2021	1507	Fine	0	0	0	20.4	16/1019	6.2

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		7/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
W#21	7/1/2021	1015	Fine	0	0	0	20.9	15/1021	2.2
	7/1/2021	1515	Fine	0	0	0	20.9	16/1019	2.2
Pit A	7/1/2021	1045	Fine	0	0	0	20.9	15/1021	3
	7/1/2021	1045	Fine	0	0	0	20.9	16/1019	3
Pit B	7/1/2021	1235	Fine	0	0	0	20.9	15/1021	8
	7/1/2021	1555	Fine	0	0	0	20.9	16/1019	8
								/	
								/	
								/	
								/	
								/	
								/	
								/	

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])	<i>[Signature]</i>	7/1/2021
Laboratory Staff:			
Checked by:			



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring -Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAEIII)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	8-1-2021	0830	Fine	0	0	0	20.9	7 / 1026	4.2
	8-1-2021	1538	Fine	0	0	0	20.9	9 / 1024	4.2
	8-1-2021	1720	Fine	0	0	0	20.9	8 / 1024	4.2
Area B	8-1-2021	0848	Fine	0	0	0	20.9	7 / 1026	2.5
	8-1-2021	1548	Fine	0	0	0	20.9	9 / 1024	2.5
	8-1-2021	1648	Fine	0	0	0	20.9	8 / 1024	2.5

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		8-1-2021
Laboratory Staff:			
Checked by:	C. Fochan (Foreman)		8-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4750	8/1/2024	0835	Fine	0	0	0	20.9	8/1026	2.5
	8/1/2024	1355	Fine	0	0	0	20.9	9/1024	2.8
CHFC 0490	8/1/2024	0900	Fine	0	0	0	20.9	8/1026	2.5
	8/1/2024	1400	Fine	0	0	0	20.9	9/1024	2.5
PAC	8/1/2024	0415	Fine	0	0	0	20.9	8/1026	8
	8/1/2024	1415	Fine	0	0	0	20.9	9/1024	8
137CHC1216	8/1/2024	0435	Fine	0	0	0	20.9	8/1026	7.1
	8/1/2024	1435	Fine	0	0	0	20.9	9/1024	7.1
137 PAC	8/1/2024	0445	Fine	0	0	0	20.9	8/1026	1.4
	8/1/2024	1445	Fine	0	0	0	20.9	9/1024	1.4
137 P3 B	8/1/2024	0455	Fine	0	0	0	20.9	8/1026	6.2
	8/1/2024	1455	Fine	0	0	0	20.9	9/1024	6.2
137 P1 A	8/1/2024	1005	Fine	0	0	0	20.9	8/1026	6.2
	8/1/2024	1505	Fine	0	0	0	20.9	9/1024	6.2

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RencPipe])		8/1/2024
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPT1	8/1/2021	1015	Fine	0	0	0	20.9	8/1026	2.2
	8/1/2021	1018	Fine	0	0	0	20.9	8/1024	2.2
Pit A	8/1/2021	1045	Fine	0	0	0	20.9	8/1026	3
	8/1/2021	1041	Fine	0	0	0	20.9	8/1024	3
Pit B	8/1/2021	1050	Fine	0	0	0	20.9	8/1026	3
	8/1/2021	1057	Fine	0	0	0	20.9	8/1024	3
								/	
								/	
								/	
								/	
								/	
								/	

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		8/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAEIII)	28 Jul 2021

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (inbar)	Remark Depth (m)
Area A	9-1-2021	0830	Fine	0	0	0	20.9	7 / 1026	4.2
	9-1-2021	1530	Fine	0	0	0	20.9	12 / 1023	4.2
	9-1-2021	1700	Fine	0	0	0	20.9	11 / 1022	4.2
Area B	9-1-2021	0845	Fine	0	0	0	20.9	7 / 1026	2.5
	9-1-2021	1345	Fine	0	0	0	20.9	12 / 1023	2.5
	9-1-2021	1645	Fine	0	0	0	20.9	11 / 1022	2.5

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		9-1-2021
Laboratory Staff:			
Checked by:	C. F. Chan (Foreman)		9-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHC 455	9/1/2021	0355	Fine	0	0	0	20.5	3/1026	2.5
	9/1/2021	1355	Fine	0	0	0	20.5	12/1023	2.5
CHC 019	9/1/2021	0900	Fine	0	0	0	20.9	8/1026	2.5
	9/1/2021	1400	Fine	0	0	0	20.9	12/1023	2.5
PFC	9/1/2021	0915	Fine	0	0	0	20.5	8/1026	3
	9/1/2021	1415	Fine	0	0	0	20.9	12/1023	3
137CHC 2466	9/1/2021	0935	Fine	0	0	0	20.9	8/1026	3.1
	9/1/2021	1435	Fine	0	0	0	20.2	12/1023	3.1
137 PFC	9/1/2021	0945	Fine	0	0	0	20.5	9/1026	1.4
	9/1/2021	1445	Fine	0	0	0	20.9	11/1023	1.4
137 PFB	9/1/2021	0955	Fine	0	0	0	20.9	9/1026	6.2
	9/1/2021	1455	Fine	0	0	0	20.9	11/1023	6.2
137 PFA	9/1/2021	1005	Fine	0	0	0	20.9	9/1026	6.2
	9/1/2021	1505	Fine	0	0	0	20.9	11/1023	6.2

Name & Designation      Signature      Date  
 Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           9/1/2021  
 Laboratory Staff:  
 Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPK1	9/1/2021	1018	Fine	0	0	0	20.9	9/1/2021	2.2
	9/1/2021	1518	Fine	0	0	0	20.9	11/1021	2.2
P1A	9/1/2021	1043	Fine	0	0	0	20.9	10/1021	3
	9/1/2021	1543	Fine	0	0	0	20.9	11/1021	3
P1B	9/1/2021	1058	Fine	0	0	0	20.9	10/1021	3
	9/1/2021	1558	Fine	0	0	0	20.9	11/1021	3
								/	
								/	
								/	
								/	
								/	
								/	

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RenoPipe])                                            9/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAEIII)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	11-1-2021	0330	Fine	0	0	0	20.9	9/1027	4.2
	11-1-2021	1330	Fine	0	0	0	20.9	9/1026	4.2
	11-1-2021	1700	Fine	0	0	0	20.9	9/1025	4.2
Area B	11-1-2021	0845	Fine	0	0	0	20.9	9/1027	2.5
	11-1-2021	1245	Fine	0	0	0	20.9	9/1026	2.5
	11-1-2021	1645	Fine	0	0	0	20.9	9/1025	2.5
							/		
							/		
							/		
							/		
							/		
							/		

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		11-1-2021
Laboratory Staff:			
Checked by:			11-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring --Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4FF0	11/1/2021	0835	Fine	0	0	0	20.9	9 / 1027	2.5
	11/1/2021	1335	Fine	0	0	0	20.9	9 / 1026	2.5
CHFC 0490	11/1/2021	0900	Fine	0	0	0	20.9	9 / 1027	2.5
	11/1/2021	1400	Fine	0	0	0	22.9	9 / 1026	2.5
Pit C	11/1/2021	0917	Fine	0	0	0	20.9	9 / 1027	8
	11/1/2021	1417	Fine	0	0	0	20.9	9 / 1028	8
197 CH.3 224	11/1/2021	0933	Fine	0	0	0	20.9	9 / 1027	7.1
	11/1/2021	1433	Fine	0	0	0	20.9	9 / 1028	7.1
191 Pit C	11/1/2021	0945	Fine	0	0	0	20.9	9 / 1028	1.4
	11/1/2021	1445	Fine	0	0	0	20.9	8 / 1028	1.4
197 Pit B	11/1/2021	0955	Fine	0	0	0	20.9	9 / 1028	6.2
	11/1/2021	1455	Fine	0	0	0	20.9	8 / 1028	6.2
197 Pit A	11/1/2021	1005	Fine	0	0	0	20.9	9 / 1028	6.2
	11/1/2021	1505	Fine	0	0	0	20.9	8 / 1028	6.2

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		11/1/2021
Laboratory Staff:			
Checked by:			



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPE1	11/1/2021	1015	Fine	0	0	0	20.9	8/1028	2.2
	11/1/2021	1315	Fine	0	0	0	20.9	8/1028	2.2
Pit A	11/1/2021	1045	Fine	0	0	0	20.9	8/1028	3
	11/1/2021	1345	Fine	0	0	0	20.9	8/1028	3
Pit B	11/1/2021	1055	Fine	0	0	0	20.9	8/1028	8
	11/1/2021	1355	Fine	0	0	0	20.9	8/1028	8
								/	
								/	
								/	
								/	
								/	
								/	

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RenoPipe])                                            11/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAEIII)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	12-1-2021	0830	Fine	0	0	0	22.9	9/1026	4.2
	12-1-2021	1330	Fine	0	0	0	22.9	15/1022	4.2
	12-1-2021	1700	Fine	0	0	0	22.9	15/1022	4.2
Area E	12-1-2021	0845	Fine	0	0	0	20.9	9/1026	2.5
	12-1-2021	1345	Fine	0	0	0	20.9	15/1022	2.5
	12-1-2021	1645	Fine	0	0	0	20.9	15/1020	2.5

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent (RenoPipe))		12-1-2021
Laboratory Staff:			
Checked by:	C. F. Chan (Foreman)		12-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
14Fc 4430	12/1/2021	0835	Fine	0	0	0	20.9	9/1026	2.5
	12/1/2021	1355	Fine	0	0	0	20.9	15/1021	2.5
14Fc 2490	12/1/2021	0900	Fine	0	0	0	20.9	9/1026	2.5
	12/1/2021	1400	Fine	0	0	0	20.9	15/1021	2.5
Pit C	12/1/2021	0915	Fine	0	0	0	20.9	10/1026	8
	12/1/2021	1415	Fine	0	0	0	20.9	15/1021	8
147CHET2611	12/1/2021	0935	Fine	0	0	0	20.9	10/1026	7.1
	12/1/2021	1435	Fine	0	0	0	20.9	15/1021	7.1
147 Pit C	12/1/2021	0945	Fine	0	0	0	20.9	10/1026	1.4
	12/1/2021	1445	Fine	0	0	0	20.9	15/1021	1.4
147 Pit B	12/1/2021	0955	Fine	0	0	0	20.9	10/1026	6.2
	12/1/2021	1455	Fine	0	0	0	20.9	15/1021	6.2
147 Pit A	12/1/2021	1005	Fine	0	0	0	20.9	10/1026	6.2
	12/1/2021	1505	Fine	0	0	0	20.9	15/1021	6.2

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		12/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPK1	12/1/2021	1018	Fine	0	0	0	20.9	11/1026	6.2
	12/1/2021	1019	Fine	0	0	0	20.9	18/1021	6.2
Pit A	12/1/2021	1045	Fine	0	0	0	20.9	12/1025	3
	12/1/2021	1548	Fine	0	0	0	20.9	18/1021	3
Pit B	12/1/2021	1055	Fine	0	0	0	20.9	12/1025	3
	12/1/2021	1555	Fine	0	0	0	20.9	18/1021	3
								/	
								/	
								/	
								/	
								/	
								/	
								/	

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		12/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE II)	29 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	13-1-2021	0830	Fine	0	0	0	20.2	11 / 1021	4.2
	13-1-2021	1330	Fine	0	0	0	20.2	17 / 1018	4.2
	13-1-2021	1700	Fine	0	0	0	20.2	17 / 1017	4.2
Area B	13-1-2021	0845	Fine	0	0	0	20.2	11 / 1021	2.5
	13-1-2021	1345	Fine	0	0	0	20.2	17 / 1018	2.5
	13-1-2021	1645	Fine	0	0	0	20.2	15 / 1017	2.5

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		13-1-2021
Laboratory Staff:			
Checked by:	C. Fokan (Foreman)		13-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4A50	13/1/2021	0235	Fine	0	0	0	20.9	12/1021	2.7
	13/1/2021	1355	Fine	0	0	0	20.9	17/1018	2.5
CHFC 2A93	13/1/2021	1400	Fine	0	0	0	20.9	12/1021	2.7
	13/1/2021	1450	Fine	0	0	0	20.9	17/1018	2.5
P17C	13/1/2021	0915	Fine	0	0	0	20.9	12/1021	8
	13/1/2021	1415	Fine	0	0	0	20.9	17/1018	8
137 PHT 2A60	13/1/2021	0435	Fine	0	0	0	20.9	13/1021	3.1
	13/1/2021	1425	Fine	0	0	0	20.9	17/1018	3.1
137 P17C	13/1/2021	0445	Fine	0	0	0	20.9	13/1021	1.4
	13/1/2021	1445	Fine	0	0	0	20.9	16/1018	1.4
137 P17B	13/1/2021	0455	Fine	0	0	0	20.9	13/1021	6.2
	13/1/2021	1455	Fine	0	0	0	20.9	16/1018	6.2
137 P17A	13/1/2021	1005	Fine	0	0	0	20.9	14/1021	6.2
	13/1/2021	1505	Fine	0	0	0	20.9	16/1018	6.2

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		13/1/2021
Laboratory Staff:			
Checked by:			

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Well 1	13/1/2021	1015	Fine	0	0	0	20.9	15/1021	2.2
	13/1/2021	1315	Fine	0	0	0	20.9	16/1018	2.2
Pit A	13/1/2021	1045	Fine	0	0	0	20.9	15/1021	3
	13/1/2021	1345	Fine	0	0	0	20.9	16/1018	3
Pit B	13/1/2021	1055	Fine	0	0	0	20.9	15/1021	3
	13/1/2021	1355	Fine	0	0	0	20.9	16/1018	3
								/	
								/	
								/	
								/	
								/	
								/	

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RenoPipe])                                            13/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAEIII)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	14-1-2021	0850	Fine	0	0	0	20.9	17 / 1019	4.2
	14-1-2021	1350	Fine	0	0	0	20.9	17 / 1016	4.2
	14-1-2021	1700	Fine	0	0	0	20.9	17 / 1016	4.2
Area B	14-1-2021	0845	Fine	0	0	0	20.9	17 / 1019	2.5
	14-1-2021	1345	Fine	0	0	0	20.9	17 / 1016	2.5
	14-1-2021	1645	Fine	0	0	0	20.9	17 / 1016	2.5

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		14-1-2021
Laboratory Staff:			
Checked by:	S. F. Chan (Foreman)		14-1-2021



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Datcs calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.FC450	14/1/2021	0833	Fine	0	0	0	20.9	14/1019	2.5
	14/1/2021	1325	Fine	0	0	0	20.9	19/1016	2.5
CH.FC 040	14/1/2021	0900	Fine	0	0	0	20.9	14/1019	2.5
	14/1/2021	1430	Fine	0	0	0	20.9	19/1016	2.5
Pit C	14/1/2021	0915	Fine	0	0	0	20.9	15/1019	3
	14/1/2021	1415	Fine	0	0	0	20.9	19/1016	3
1370401261	14/1/2021	0935	Fine	0	0	0	20.9	15/1019	3.1
	14/1/2021	1435	Fine	0	0	0	20.9	19/1016	3.1
137 Pit C	14/1/2021	0945	Fine	0	0	0	20.9	15/1019	1.4
	14/1/2021	1445	Fine	0	0	0	20.9	19/1016	1.4
137 Pit B	14/1/2021	0955	Fine	0	0	0	20.9	16/1019	8.6
	14/1/2021	1455	Fine	0	0	0	20.9	19/1016	8.6
137 Pit A	14/1/2021	1005	Fine	0	0	0	20.9	17/1019	2.3
	14/1/2021	1507	Fine	0	0	0	20.9	19/1016	2.3

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		14/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR 1	16/1/2021	1015	Fine	0	0	0	20.9	17/1019	2.2
	14/1/2021	1515	Fine	0	0	0	20.9	19/1016	2.2
CHA 570	14/1/2021	1025	Fine	0	0	0	20.9	17/1019	0.6
	14/1/2021	1503	Fine	0	0	0	20.9	19/1016	0.6
WPR 3	14/1/2021	1037	Fine	0	0	0	20.9	17/1019	0.6
	16/1/2021	1535	Fine	0	0	0	20.9	19/1016	0.6
PIT A	14/1/2021	1045	Fine	0	0	0	20.9	17/1019	3
	14/1/2021	1545	Fine	0	0	0	20.9	18/1016	3
PIT B	14/1/2021	1055	Fine	0	0	0	20.9	17/1019	8
	14/1/2021	1555	Fine	0	0	0	20.9	18/1016	8

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           14/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAEIII)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	15-1-221	0830	Fine	0	0	0	20.9	15/1018	4.2
	15-1-221	1530	Fine	0	0	0	20.9	21/1014	4.2
	15-1-221	1750	Fine	0	0	0	20.9	20/1014	4.2
Area B	15-1-221	0845	Fine	0	0	0	20.9	15/1018	2.5
	15-1-221	1745	Fine	0	0	0	20.9	21/1014	2.5
	15-1-221	1845	Fine	0	0	0	20.9	20/1014	2.5

	Name & Designation	Signature	Date
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		15-1-2021
Laboratory Staff:			
Checked by:	of-cham (Foreman)		15-1-2021

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.Fc 4770	15/1/2021	0835	Fine	0	0	0	20.9	16/1018	2.8
	15/1/2021	1355	Fine	0	0	0	20.9	22/1014	2.8
CH.Fc 0490	15/1/2021	0900	Fine	0	0	0	20.9	16/1018	2.8
	15/1/2021	1420	Fine	0	0	0	20.9	22/1014	2.8
Pit C	15/1/2021	0915	Fine	0	0	0	20.9	16/1018	8
	15/1/2021	1435	Fine	0	0	0	20.9	22/1014	8
137 CHC 0466	15/1/2021	0935	Fine	0	0	0	20.9	17/1018	3.1
	15/1/2021	1455	Fine	0	0	0	20.9	22/1014	3.1
137 Pit C	15/1/2021	0945	Fine	0	0	0	20.9	17/1018	1.4
	15/1/2021	1505	Fine	0	0	0	20.9	21/1014	1.4
137 Pit B	15/1/2021	0955	Fine	0	0	0	20.9	18/1018	8.6
	15/1/2021	1455	Fine	0	0	0	20.9	21/1014	8.6
137 Pit A	15/1/2021	1005	Fine	0	0	0	20.9	18/1018	8.3
	15/1/2021	1505	Fine	0	0	0	20.9	21/1014	8.3

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           15/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPE1	15/1/2021	1017	Fine	0	0	0	20.9	18/1017	2.2
	15/1/2021	1518	Fine	0	0	0	20.9	21/1014	2.2
CHA 5#70	15/1/2021	1025	Fine	0	0	0	20.9	18/1017	0.6
	15/1/2021	1525	Fine	0	0	0	20.9	21/1014	0.6
WPE 3	15/1/2021	1032	Fine	0	0	0	20.9	18/1017	0.6
	15/1/2021	1532	Fine	0	0	0	20.9	21/1014	0.6
Pit A	15/1/2021	1044	Fine	0	0	0	20.9	19/1017	3
	15/1/2021	1544	Fine	0	0	0	20.9	21/1014	3
Pit B	15/1/2021	1052	Fine	0	0	0	20.9	19/1017	8
	15/1/2021	1552	Fine	0	0	0	20.9	21/1014	8
								/	
								/	
								/	

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           15/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAEIII)	29 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (atbar)	Remark Depth (m)
Area A	16-1-2021	0830	Fine	0	0	0	20.9	16 / 1018	4.0
	16-1-2021	1330	Fine	0	0	0	20.9	20 / 1016	4.0
	16-1-2021	1730	Fine	0	0	0	20.9	18 / 1016	4.0
Area B	16-1-2021	0845	Fine	0	0	0	20.9	16 / 1018	2.5
	16-1-2021	1345	Fine	0	0	0	20.9	20 / 1016	2.5
	16-1-2021	1645	Fine	0	0	0	20.9	18 / 1016	2.5

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Eric Man (Sub-Agent [RenoPipe])		16-1-2021
Laboratory Staff:			
Checked by:	C. F. Chan (Foreman)		16-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4750	16/1/2021	0835	Fine	0	0	0	20.9	17/1018	2.5
	16/1/2021	1355	Fine	0	0	0	20.9	20/1016	2.5
11A FC 2490	16/1/2021	0900	Fine	0	0	0	20.9	17/1016	2.7
	16/1/2021	1430	Fine	0	0	0	20.9	20/1016	2.5
Px c	16/1/2021	0915	Fine	0	0	0	20.9	18/1018	8
	16/1/2021	1415	Fine	0	0	0	20.9	20/1015	8
137 CHC72466	16/1/2021	0935	Fine	0	0	0	20.9	18/1018	2.1
	16/1/2021	1435	Fine	0	0	0	20.9	19/1015	2.1
137 PxC	16/1/2021	0945	Fine	0	0	0	20.9	19/1018	1.4
	16/1/2021	1445	Fine	0	0	0	20.9	19/1015	1.4
137 PxB	16/1/2021	0955	Fine	0	0	0	20.9	19/1018	8.6
	16/1/2021	1455	Fine	0	0	0	20.9	19/1015	8.6
137 PxA	16/1/2021	1005	Fine	0	0	0	20.9	19/1018	8.3
	16/1/2021	1505	Fine	0	0	0	20.9	19/1015	8.3

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RenoPipe])                                            16/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WR 1	16/1/2021	1015	Fine	0	0	0	20.9	19/1015	2.2
	16/1/2021	1515	Fine	0	0	0	20.9	19/1015	2.2
WR 2	16/1/2021	1215	Fine	0	0	0	20.9	19/1015	2.2
	16/1/2021	1525	Fine	0	0	0	20.9	19/1015	2.2
WR 3	16/1/2021	1035	Fine	0	0	0	20.9	20/1015	0.6
	16/1/2021	1535	Fine	0	0	0	20.9	19/1015	0.6
Pit A	16/1/2021	1045	Fine	0	0	0	20.9	20/1015	3
	16/1/2021	1545	Fine	0	0	0	20.9	19/1015	3
Pit B	16/1/2021	1055	Fine	0	0	0	20.9	20/1015	8
	16/1/2021	1555	Fine	0	0	0	20.9	19/1015	8

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RencPipe])                                            16/1/2021

Laboratory Staff:

Checked by:



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	18-1-2021	0830	Fine	0	0	0	20.9	11/1020	4.2
	18-1-2021	1330	Fine	0	0	0	20.9	17/1020	4.2
	18-1-2021	1700	Fine	0	0	0	20.9	16/1020	4.2
Area B	18-1-2021	0840	Fine	0	0	0	20.9	11/1020	2.5
	18-1-2021	1540	Fine	0	0	0	20.9	17/1021	2.5
	18-1-2021	1640	Fine	0	0	0	20.9	16/1020	2.5

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		18-1-2021
Laboratory Staff:			
Checked by:	C.F. Chan (Inspector)		18-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4H30	18/1/2021	0855	Fine	0	0	0	20.9	12/1025	2.5
	18/1/2021	1355	Fine	0	0	0	20.9	17/1024	2.5
CHFC 0490	18/1/2021	0900	Fine	0	0	0	20.9	12/1025	2.5
	18/1/2021	1400	Fine	0	0	0	20.9	17/1024	2.5
PATC	18/1/2021	0917	Fine	0	0	0	20.9	12/1025	8
	18/1/2021	1415	Fine	0	0	0	20.9	17/1024	8
137 CHIT266	18/1/2021	0958	Fine	0	0	0	20.9	12/1025	2.1
	18/1/2021	1453	Fine	0	0	0	20.9	17/1024	2.1
137 PATC	18/1/2021	0945	Fine	0	0	0	20.9	13/1025	1.4
	18/1/2021	1458	Fine	0	0	0	20.9	17/1024	1.4
137 PATB	18/1/2021	0937	Fine	0	0	0	20.9	13/1025	8.6
	18/1/2021	1455	Fine	0	0	0	20.9	17/1024	8.6
137 PATA	18/1/2021	1005	Fine	0	0	0	20.9	13/1025	8.3
	18/1/2021	1505	Fine	0	0	0	20.9	17/1024	8.3

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		18/1/2021
Laboratory Staff:			
Checked by:			

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Pen'ia-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WRE 1	18/1/2021	1015	Fine	0	0	0	22.9	14/1025	2.2
	18/1/2021	1015	Fine	0	0	0	22.9	17/1020	2.2
CHA 270	18/1/2021	1025	Fine	0	0	0	22.9	14/1025	2.8
	18/1/2021	1025	Fine	0	0	0	22.9	17/1020	2.3
WRE 3	18/1/2021	1035	Fine	0	0	0	22.9	14/1025	0.6
	18/1/2021	1035	Fine	0	0	0	22.9	17/1020	0.6
Pit A	18/1/2021	1045	Fine	0	0	0	22.9	14/1025	5
	18/1/2021	1045	Fine	0	0	0	22.9	17/1020	5
Pit B	18/1/2021	1055	Fine	0	0	0	22.9	17/1025	8
	18/1/2021	1055	Fine	0	0	0	22.9	17/1020	8

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           18/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	19-1-2021	0838	Fine	0	0	0	20.9	14/1022	4.2
	19-1-2021	1330	Fine	0	0	0	20.9	17/1019	4.2
Area B	19-1-2021	1700	Fine	0	0	0	20.9	16/1019	4.2
	19-1-2021	0845	Fine	0	0	0	20.9	14/1022	2.5
	19-1-2021	1345	Fine	0	0	0	20.9	17/1019	2.5
	19-1-2021	1645	Fine	0	0	0	20.9	16/1019	2.5

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		19-1-2021
Laboratory Staff:			
Checked by:	C.F. Chan (Foreman) 19-1-2021		

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4A	19/1/2021	0855	Fine	0	0	0	20.9	14/1022	2.5
	19/1/2021	1355	Fine	0	0	0	20.9	17/1020	2.5
CHFC 0493	19/1/2021	0900	Fine	0	0	0	20.9	14/1022	2.5
	19/1/2021	1400	Fine	0	0	0	20.9	17/1020	2.5
PFC	19/1/2021	0915	Fine	0	0	0	20.9	14/1022	8
	19/1/2021	1415	Fine	0	0	0	20.9	17/1019	8
137CHT2+66	19/1/2021	0935	Fine	0	0	0	20.9	15/1022	7.1
	19/1/2021	1435	Fine	0	0	0	20.9	17/1019	7.1
137 PFC	19/1/2021	0945	Fine	0	0	0	20.9	15/1022	1.4
	19/1/2021	1445	Fine	0	0	0	20.9	17/1019	1.4
137 PFC B	19/1/2021	0955	Fine	0	0	0	20.9	15/1022	8.6
	19/1/2021	1455	Fine	0	0	0	20.9	17/1019	8.6
137 PFC A	19/1/2021	1005	Fine	0	0	0	20.9	15/1022	8.3
	19/1/2021	1505	Fine	0	0	0	20.9	17/1019	8.3

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		19/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR 1	19/1/2021	1015	Fine	0	0	0	22.9	16/1022	2.2
	19/1/2021	1018	Fine	0	0	0	22.9	16/1019	2.2
CHA 5+70	19/1/2021	1025	Fine	0	0	0	22.9	16/1022	2.8
	19/1/2021	1528	Fine	0	0	0	22.9	16/1019	2.8
WPR 3	19/1/2021	1037	Fine	0	0	0	22.9	16/1022	2.6
	19/1/2021	1538	Fine	0	0	0	22.9	16/1019	2.6
Pit A	19/1/2021	1047	Fine	0	0	0	22.9	16/1022	5
	19/1/2021	1547	Fine	0	0	0	22.9	16/1019	5
Pit B	19/1/2021	1057	Fine	0	0	0	22.9	16/1022	8
	19/1/2021	1557	Fine	0	0	0	22.9	16/1019	8
								/	
								/	
								/	

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           19/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	20-1-2021	0830	Fine	0	0	0	20.9	17/1020	4.2
	20-1-2021	1530	Fine	0	0	0	20.9	21/1017	4.2
	20-1-2021	1720	Fine	0	0	0	20.9	19/1016	4.2
Area B	20-1-2021	0845	Fine	0	0	0	20.9	17/1020	2.5
	20-1-2021	1345	Fine	0	0	0	20.9	21/1017	2.5
	20-1-2021	1645	Fine	0	0	0	20.9	19/1016	2.5

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])	<i>[Signature]</i>	20-1-2021
Laboratory Staff:			
Checked by:	<i>[Signature]</i> (Foreman)	<i>[Signature]</i>	20-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.FC 477	20/1/2021	0830	Fine	0	0	0	20.9	17/1020	2.5
	20/1/2021	1330	Fine	0	0	0	20.9	21/1017	2.5
CH.FC 0490	20/1/2021	0900	Fine	0	0	0	20.9	17/1020	2.5
	20/1/2021	1400	Fine	0	0	0	20.6	21/1016	2.5
P+C	20/1/2021	0910	Fine	0	0	0	20.5	17/1020	8
	20/1/2021	1410	Fine	0	0	0	20.9	21/1016	8
191CHCT 248	20/1/2021	0950	Fine	0	0	0	20.9	17/1020	3.1
	20/1/2021	1430	Fine	0	0	0	20.9	21/1016	3.1
191 P+C	20/1/2021	0940	Fine	0	0	0	20.9	17/1020	1.4
	20/1/2021	1440	Fine	0	0	0	20.7	21/1016	1.4
197 P+A B	20/1/2021	0950	Fine	0	0	0	20.9	17/1020	8.6
	20/1/2021	1450	Fine	0	0	0	20.9	21/1016	8.6
197 P+A	20/1/2021	1000	Fine	0	0	0	20.9	18/1020	8.3
	20/1/2021	1500	Fine	0	0	0	20.9	21/1016	8.3

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])      *[Signature]*      20/1/2021

Laboratory Staff:

Checked by:



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WYR1	20/1/2021	1015	Fine	0	0	0	20.9	18/1020	2.2
	20/1/2021	1515	Fine	0	0	0	20.9	21/1016	2.2
CHAR 5*70	20/1/2021	1025	Fine	0	0	0	20.9	19/1020	2.8
	20/1/2021	1515	Fine	0	0	0	20.9	21/1016	2.8
WYR3	20/1/2021	1035	Fine	0	0	0	20.9	19/1020	1.1
	20/1/2021	1535	Fine	0	0	0	20.9	21/1016	1.1
P*1A	20/1/2021	1045	Fine	0	0	0	20.9	19/1020	5
	20/1/2021	1545	Fine	0	0	0	20.9	21/1016	5
P*1B	20/1/2021	1055	Fine	0	0	0	20.9	19/1020	8
	20/1/2021	1555	Fine	0	0	0	20.9	21/1016	8
								/	
								/	
								/	

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           20/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	21-1-2021	0830	Fine	0	0	0	20.9	19 / 1017	4.2
	21-1-2021	1330	Fine	0	0	0	20.9	22 / 1014	4.2
Area B	21-1-2021	1700	Fine	0	0	0	20.9	22 / 1014	4.2
	21-1-2021	0845	Fine	0	0	0	20.9	19 / 1017	2.5
	21-1-2021	1345	Fine	0	0	0	20.9	22 / 1014	2.5
	21-1-2021	1645	Fine	0	0	0	20.9	22 / 1014	2.5

Name & Designation      Signature      Date  
 Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])      *[Signature]*      21-1-2021

Laboratory Staff:

Checked by:      *C. F. Chan (Foreman) [Signature]*      21-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC470	21/1/2021	0855	Fine	0	0	0	20.9	20 / 1017	2.5
	21/1/2021	1355	Fine	0	0	0	20.9	22 / 1014	2.5
CHFC 0740	21/1/2021	0920	Fine	0	0	0	20.9	20 / 1017	2.5
	21/1/2021	1420	Fine	0	0	0	20.9	22 / 1014	2.5
P7C	21/1/2021	0910	Fine	0	0	0	20.9	20 / 1017	3
	21/1/2021	1415	Fine	0	0	0	20.9	22 / 1014	3
137CHC2160	21/1/2021	0935	Fine	0	0	0	20.9	20 / 1017	7.1
	21/1/2021	1435	Fine	0	0	0	20.9	22 / 1013	7.1
137 P7 C	21/1/2021	0940	Fine	0	0	0	20.9	20 / 1017	1.4
	21/1/2021	1440	Fine	0	0	0	20.9	22 / 1013	1.4
137 P7 B	21/1/2021	0955	Fine	0	0	0	20.9	20 / 1017	8.6
	21/1/2021	1455	Fine	0	0	0	20.9	22 / 1013	8.6
137 P7 A	21/1/2021	1005	Fine	0	0	0	20.9	21 / 1017	8.3
	21/1/2021	1505	Fine	0	0	0	20.9	22 / 1013	8.3

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer (RenoPipe))		21/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (GRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPR1	21/1/2021	1013	Fine	0	0	0	20.9	21/1019	2.2
	21/1/2021	1513	Fine	0	0	0	20.9	22/1013	2.2
CHAAD10	21/1/2021	1025	Fine	0	0	0	20.9	21/1019	2.8
	21/1/2021	1525	Fine	0	0	0	20.9	22/1019	2.8
WPR3	21/1/2021	1035	Fine	0	0	0	20.9	21/1019	1.1
	21/1/2021	1535	Fine	0	0	0	20.9	22/1019	1.1
Pit A	21/1/2021	1045	Fine	0	0	0	20.9	21/1019	5
	21/1/2021	1545	Fine	0	0	0	20.9	22/1019	5
Pit B	21/1/2021	1055	Fine	0	0	0	20.9	21/1019	8
	21/1/2021	1555	Fine	0	0	0	20.9	22/1019	8
								/	
								/	
								/	

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RenoPipe])                                            21/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring --Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	22-1-2021	0830	Fine	0	0	0	20.9	19/1015	4.2
	22-1-2021	1330	Fine	0	0	0	20.5	23/1012	4.2
	22-1-2021	1700	Fine	0	0	0	20.9	24/1011	4.2
Area B	22-1-2021	0845	Fine	0	0	0	20.9	19/1015	2.5
	22-1-2021	1345	Fine	0	0	0	20.9	23/1012	2.5
	22-1-2021	1645	Fine	0	0	0	20.9	24/1011	2.5

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])      *[Signature]*      22-1-2021

Laboratory Staff:

Checked by:      *[Signature]*      *[Signature]*      22-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4470	22/1/2021	0855	Fine	0	0	0	20.9	19/1015	2.5
	22/1/2021	1655	Fine	0	0	0	20.9	24/1016	2.5
CHFC 0292	22/1/2021	0100	Fine	0	0	0	20.9	19/1015	2.5
	22/1/2021	1400	Fine	0	0	0	20.9	24/1016	2.5
P:TC	22/1/2021	0918	Fine	0	0	0	20.9	19/1016	8
	22/1/2021	1418	Fine	0	0	0	20.9	24/1011	8
137 CHC 2466	22/1/2021	0937	Fine	0	0	0	20.9	19/1016	7.1
	22/1/2021	1437	Fine	0	0	0	20.9	24/1011	7.1
137 P:TC	22/1/2021	0949	Fine	0	0	0	20.9	20/1016	1.4
	22/1/2021	1449	Fine	0	0	0	20.9	24/1011	1.4
137 P:TC	22/1/2021	0955	Fine	0	0	0	20.9	20/1016	8.6
	22/1/2021	1455	Fine	0	0	0	20.9	24/1011	8.6
137 P:TC	22/1/2021	1205	Fine	0	0	0	20.9	21/1016	8.3
	22/1/2021	1505	Fine	0	0	0	20.9	24/1011	8.3

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer (RenoPipe))		22/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WR 1	22/1/2021	1018	Fine	0	0	0	20.9	21/1016	2.2
	22/1/2021	1818	Fine	0	0	0	20.9	28/1011	2.2
CHA 5+7	22/1/2021	1028	Fine	0	0	0	20.9	21/1016	2.8
	22/1/2021	1828	Fine	0	0	0	20.9	25/1011	2.8
WR 3	22/1/2021	1038	Fine	0	0	0	20.9	21/1016	1.1
	22/1/2021	1838	Fine	0	0	0	20.9	28/1011	1.1
Pit A	22/1/2021	1048	Fine	0	0	0	20.9	21/1016	5
	22/1/2021	1848	Fine	0	0	0	20.9	28/1011	5
Pit B	22/1/2021	1058	Fine	0	0	0	20.9	21/1016	8
	22/1/2021	1858	Fine	0	0	0	20.9	28/1011	8
								/	
								/	
								/	

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer (RenoPipe))                                            22/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	23-1-2021	0830	Fine	0	0	0	20.9	19 / 1015	4.2
	23-1-2021	1330	Fine	0	0	0	20.9	24 / 1013	4.2
	23-1-2021	1700	Fine	0	0	0	20.9	21 / 1013	4.2
Area B	23-1-2021	0845	Fine	0	0	0	20.9	19 / 1015	2.5
	23-1-2021	1345	Fine	0	0	0	20.9	24 / 1013	2.5
	23-1-2021	1645	Fine	0	0	0	20.9	21 / 1013	2.5

Name & Designation      Signature      Date  
 Field Operator:      Tng Wai Kin (Safety Officer [RenoPipe])      *[Signature]*      23-1-2021

Laboratory Staff:

Checked by:      *[Signature]*      23-1-2021.



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 440	23/1/2021	0835	Fine	0	0	0	20.9	19/1015	2.5
	23/1/2021	1337	Fine	0	0	0	20.9	24/1013	2.5
CHFC 0490	23/1/2021	0900	Fine	0	0	0	20.9	19/1015	2.5
	23/1/2021	1400	Fine	0	0	0	20.9	24/1013	2.5
Pit C	23/1/2021	0917	Fine	0	0	0	20.9	19/1015	8
	23/1/2021	1415	Fine	0	0	0	20.9	23/1013	8
137 CHFC266	23/1/2021	0937	Fine	0	0	0	20.9	19/1016	2.1
	23/1/2021	1435	Fine	0	0	0	20.9	23/1013	2.1
137 P.A.C	23/1/2021	0940	Fine	0	0	0	20.9	19/1016	1.4
	23/1/2021	1435	Fine	0	0	0	20.9	23/1013	1.4
137 P.T.B	23/1/2021	0957	Fine	0	0	0	20.9	20/1018	8.6
	23/1/2021	1437	Fine	0	0	0	20.9	23/1013	8.6
137 P.T.A	23/1/2021	1005	Fine	0	0	0	20.9	20/1018	8.3
	23/1/2021	1505	Fine	0	0	0	20.9	23/1013	8.3

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		23/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WPE 1	23/1/2021	1015	Fine	0	0	0	20.9	20/1015	2.2
	23/1/2021	1015	Fine	0	0	0	20.9	23/1015	2.2
CHA 5770	23/1/2021	1025	Fine	0	0	0	20.9	21/1015	2.8
	23/1/2021	1525	Fine	0	0	0	20.9	25/1015	2.8
WPE 3	23/1/2021	1035	Fine	0	0	0	20.9	21/1015	1.1
	23/1/2021	1535	Fine	0	0	0	20.9	22/1015	1.1
Pit A	23/1/2021	1045	Fine	0	0	0	20.9	21/1015	5
	23/1/2021	1545	Fine	0	0	0	20.9	22/1015	5
Pit B	23/1/2021	1055	Fine	0	0	0	20.9	22/1015	8
	23/1/2021	1555	Fine	0	0	0	20.9	22/1015	8

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RencPipe])           23/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	25-1-2021	0830	Fine	0	0	0	20.9	17 / 1019	4.2
	25-1-2021	1330	Fine	0	0	0	20.9	22 / 1017	4.2
	25-1-2021	1700	Fine	0	0	0	20.9	21 / 1016	4.2
Area B	25-1-2021	0845	Fine	0	0	0	20.9	17 / 1019	2.5
	25-1-2021	1345	Fine	0	0	0	20.9	22 / 1017	2.5
	25-1-2021	1645	Fine	0	0	0	20.9	21 / 1016	2.5

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [Renopipe])		25-1-2021
Laboratory Staff:			
Checked by:	C.F. Chan (Foreman)		25-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CH.FC 470	25/1/2021	0835	Fine	0	0	0	20.9	17 / 1020	2.5
	25/1/2021	1325	Fine	0	0	0	20.9	23 / 1016	2.5
CH.FC 0760	25/1/2021	0900	Fine	0	0	0	20.9	17 / 1020	2.5
	25/1/2021	1400	Fine	0	0	0	20.9	23 / 1016	2.5
PFC	25/1/2021	0915	Fine	0	0	0	20.9	18 / 1020	8
	25/1/2021	1415	Fine	0	0	0	20.9	22 / 1016	8
PFC 206	25/1/2021	0935	Fine	0	0	0	20.9	18 / 1020	7.1
	25/1/2021	1435	Fine	0	0	0	20.9	22 / 1016	7.1
PFC	25/1/2021	0945	Fine	0	0	0	20.9	18 / 1020	1.4
	25/1/2021	1445	Fine	0	0	0	20.9	22 / 1016	1.4
PFC	25/1/2021	0955	Fine	0	0	0	20.9	18 / 1020	8.6
	25/1/2021	1455	Fine	0	0	0	20.9	22 / 1016	8.6
PFC A	25/1/2021	1005	Fine	0	0	0	20.9	19 / 1020	8.3
	25/1/2021	1505	Fine	0	0	0	20.9	22 / 1016	8.3

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           25/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WRF1	25/1/2021	1015	Fine	0	0	0	20.9	19/1020	2.2
		1515	Fine	0	0	0	20.9	22/1016	2.2
CHH 5+7+9	25/1/2021	1025	Fine	0	0	0	20.9	20/1020	2.3
		1525	Fine	0	0	0	20.9	22/1016	2.3
Pit A	25/1/2021	1045	Fine	0	0	0	20.9	20/1020	5
		1545	Fine	0	0	0	20.9	22/1016	5
Pit B	25/1/2021	1055	Fine	0	0	0	20.9	20/1020	8
		1555	Fine	0	0	0	20.9	22/1016	8

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RencPipe])                                            25/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	26-1-2021	0930	Fine	0	0	0	20.9	17 / 1014	4.2
	26-1-2021	1330	Fine	0	0	0	20.9	25 / 1016	4.2
	26-1-2021	1700	Fine	0	0	0	20.9	29 / 1015	4.2
Area B	26-1-2021	0845	Fine	0	0	0	20.9	17 / 1014	2.5
	26-1-2021	1345	Fine	0	0	0	22.9	23 / 1016	2.5
	26-1-2021	1645	Fine	0	0	0	20.9	21 / 1015	2.5

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		26-1-2021
Laboratory Staff:			
Checked by:	C. F. Chan (Foreman)		26-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 415	26/1/2021	0857	Fine	0	0	0	20.9	18/1019	2.5
CHFC 415	26/1/2021	1357	Fine	0	0	0	20.9	23/1015	2.5
CHFC 415	26/1/2021	0900	Fine	0	0	0	20.9	18/1019	2.5
CHFC 415	26/1/2021	1450	Fine	0	0	0	20.9	22/1015	2.5
P17C	26/1/2021	0917	Fine	0	0	0	20.9	18/1019	8
P17C	26/1/2021	1417	Fine	0	0	0	20.9	22/1015	8
P17C	26/1/2021	1937	Fine	0	0	0	20.9	18/1019	7.1
P17C	26/1/2021	1437	Fine	0	0	0	20.9	22/1015	7.1
P17C	26/1/2021	0947	Fine	0	0	0	20.9	19/1019	2.2
P17C	26/1/2021	1447	Fine	0	0	0	20.9	22/1015	2.2
P17C	26/1/2021	0957	Fine	0	0	0	20.9	19/1019	8.6
P17C	26/1/2021	1457	Fine	0	0	0	20.9	22/1015	8.6
P17C	26/1/2021	1007	Fine	0	0	0	20.9	19/1019	8.3
P17C	26/1/2021	1707	Fine	0	0	0	20.9	22/1015	8.3

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		26/1/2021
Laboratory Staff:			
Checked by:			

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WR1	26/1/2021	1015	Fine	0	0	0	20.9	19/1019	2.2
	26/1/2021	1515	Fine	0	0	0	20.9	22/1015	2.2
CHA 5470	26/1/2021	1025	Fine	0	0	0	20.9	20/1019	2.8
	26/1/2021	1525	Fine	0	0	0	20.9	22/1015	2.8
Pit A	26/1/2021	1045	Fine	0	0	0	20.9	20/1019	5
	26/1/2021	1545	Fine	0	0	0	20.9	22/1015	5
Pit B	26/1/2021	1055	Fine	0	0	0	20.9	21/1019	8
	26/1/2021	1555	Fine	0	0	0	20.9	22/1015	8
								/	
								/	
								/	
								/	
								/	

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		26/1/2021
Laboratory Staff:			
Checked by:			



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	27-1-2021	0830	Fine	0	0	0	20.9	17 / 1010	4.2
	27-1-2021	1330	Fine	0	0	0	20.9	21 / 1017	4.2
	27-1-2021	1700	Fine	0	0	0	20.9	19 / 1016	4.2
Area B	27-1-2021	0845	Fine	0	0	0	20.9	17 / 1020	2.5
	27-1-2021	1345	Fine	0	0	0	20.9	21 / 1017	2.5
	27-1-2021	1645	Fine	0	0	0	20.9	19 / 1016	2.5

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [RencPipe])		27-1-2021
Laboratory Staff:			
Checked by:	C. F. Chan (Foreman)		27-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4670	27/1/2021	0855	Fine	0	0	0	20.9	17/1020	2.5
	27/1/2021	1355	Fine	0	0	0	20.9	21/1017	2.5
CHFC 0790	27/1/2021	0900	Fine	0	0	0	20.9	17/1020	2.5
	27/1/2021	1400	Fine	0	0	0	20.9	21/1017	2.5
Pit C	27/1/2021	0915	Fine	0	0	0	20.9	17/1020	2
	27/1/2021	1415	Fine	0	0	0	20.9	21/1016	2
1370ACT 266	27/1/2021	0955	Fine	0	0	0	20.9	18/1020	2.1
	27/1/2021	1435	Fine	0	0	0	20.9	20/1016	2.1
1370A C	27/1/2021	0955	Fine	0	0	0	20.9	18/1020	2.2
	27/1/2021	1445	Fine	0	0	0	20.9	20/1016	2.2
1370A B	27/1/2021	0955	Fine	0	0	0	20.9	18/1020	8.6
	27/1/2021	1455	Fine	0	0	0	20.9	20/1016	8.6
1370A A	27/1/2021	1005	Fine	0	0	0	20.9	18/1020	8.3
	27/1/2021	1505	Fine	0	0	0	20.9	20/1016	8.3

Name & Designation      Signature      Date  
 Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           27/1/2021  
 Laboratory Staff:  
 Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
W21	27/1/2021	1015	Fine	0	0	0	20.9	18/1020	2.2
	27/1/2021	1015	Fine	0	0	0	20.9	20/1010	2.2
CHA 372	27/1/2021	1025	Fine	0	0	0	20.9	18/1020	2.3
	27/1/2021	1025	Fine	0	0	0	20.9	20/1010	2.3
V1A	27/1/2021	1045	Fine	0	0	0	20.9	18/1020	5
	27/1/2021	1045	Fine	0	0	0	20.9	20/1010	5
V1B	27/1/2021	1055	Fine	0	0	0	20.9	19/1020	3
	27/1/2021	1055	Fine	0	0	0	20.9	20/1010	3
								/	
								/	
								/	
								/	
								/	

Name & Designation      Signature      Date

Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])      *[Signature]*      27/1/2021

Laboratory Staff:

Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	28-1-2021	0830	Fine	0	0	0	20.9	17 / 1022	4.2
	28-1-2021	1330	Fine	0	0	0	20.9	23 / 1020	4.2
	28-1-2021	1700	Fine	0	0	0	20.9	22 / 1019	4.2
Area B	28-1-2021	0845	Fine	0	0	0	20.9	17 / 1022	2.5
	28-1-2021	1345	Fine	0	0	0	20.9	23 / 1020	2.5
	28-1-2021	1645	Fine	0	0	0	20.9	22 / 1019	2.5

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer (RenoPipe))		28-1-2021
Laboratory Staff:			
Checked by:	C. F. Chan (Foreman)		28-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring --Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 430	28/1/2021	0835	Fine	0	0	0	20.9	17/1022	2.5
	28/1/2021	1355	Fine	0	0	0	20.9	23/1019	2.5
CHFC 0740	28/1/2021	0600	Fine	0	0	0	20.9	17/1022	2.5
	28/1/2021	1400	Fine	0	0	0	20.9	23/1019	2.5
Pit C	28/1/2021	0915	Fine	0	0	0	20.9	17/1022	8
	28/1/2021	1415	Fine	0	0	0	20.9	23/1019	8
P97 CHFC 266	28/1/2021	0935	Fine	0	0	0	20.9	18/1022	2.1
	28/1/2021	1435	Fine	0	0	0	20.9	22/1019	2.1
P97 Pit C	28/1/2021	0945	Fine	0	0	0	20.9	18/1022	2.2
	28/1/2021	1445	Fine	0	0	0	20.9	22/1019	2.2
P97 Pit B	28/1/2021	0955	Fine	0	0	0	20.9	18/1022	8.6
	28/1/2021	1455	Fine	0	0	0	20.9	22/1019	8.6
P97 Pit A	28/1/2021	1005	Fine	0	0	0	20.9	18/1022	8.3
	28/1/2021	1505	Fine	0	0	0	20.9	22/1019	8.3

Name & Designation      Signature      Date  
 Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           28/1/2021  
 Laboratory Staff:  
 Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Well 1	28/1/2021	1015	Fine	0	0	0	20.9	19/1022	2.2
	28/1/2021	1315	Fine	0	0	0	20.9	22/1019	2.2
CHA 5770	28/1/2021	1025	Fine	0	0	0	20.9	19/1022	2.8
	28/1/2021	1525	Fine	0	0	0	20.9	22/1019	2.8
Pit A	28/1/2021	1045	Fine	0	0	0	20.9	19/1022	5
	28/1/2021	1545	Fine	0	0	0	20.9	22/1019	5
Pit B	28/1/2021	1055	Fine	0	0	0	20.9	19/1022	5
	28/1/2021	1555	Fine	0	0	0	20.9	22/1019	5
								/	
								/	
								/	
								/	
								/	

Name & Designation      Signature      Date  
 Field Operator:      Ting Wai Kin (Safety Officer [RenoPipe])           28/1/2021  
 Laboratory Staff:  
 Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	24-1-2021	0830	Fine	0	0	0	20.9	15 / 1024	4.2
	24-1-2021	1330	Fine	0	0	0	20.9	18 / 1022	4.2
	24-1-2021	1700	Fine	0	0	0	20.9	17 / 1024	4.2
Area B	24-1-2021	0845	Fine	0	0	0	20.9	15 / 1024	2.5
	24-1-2021	1345	Fine	0	0	0	20.9	18 / 1022	2.5
	24-1-2021	1645	Fine	0	0	0	20.9	17 / 1024	2.5

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		24-1-2021
Laboratory Staff:			
Checked by:	C. Fok (EPA)		24-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4830	29/1/2021	0835	Fine	0	0	0	20.9	15/1024	2.5
	29/1/2021	1358	Fine	0	0	0	20.9	18/1022	2.5
CHFC 0490	29/1/2021	0900	Fine	0	0	0	20.9	15/1024	2.5
	29/1/2021	1420	Fine	0	0	0	20.9	18/1022	2.5
P.F.C	29/1/2021	0915	Fine	0	0	0	20.9	15/1024	8
	29/1/2021	1415	Fine	0	0	0	20.9	18/1021	8
P9 CHFC 246	29/1/2021	0930	Fine	0	0	0	20.9	16/1024	2.1
	29/1/2021	1435	Fine	0	0	0	20.9	18/1021	2.1
P7 P.F.C	29/1/2021	0940	Fine	0	0	0	20.9	16/1024	2.2
	29/1/2021	1450	Fine	0	0	0	20.9	18/1021	2.2
P9 P.F.C	29/1/2021	0955	Fine	0	0	0	20.9	16/1024	8.6
	29/1/2021	1455	Fine	0	0	0	20.9	18/1021	8.6
P7 P.F.C A	29/1/2021	1005	Fine	0	0	0	20.9	16/1024	8.3
	29/1/2021	1505	Fine	0	0	0	20.9	18/1021	8.3

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipes])		29/1/2021
Laboratory Staff:			
Checked by:			

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT



**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
W121	29/1/2021	1015	Fine	0	0	0	20.9	16/1024	2.2
	29/1/2021	1515	Fine	0	0	0	20.9	18/1021	2.2
CHA 5170	29/1/2021	1025	Fine	0	0	0	20.9	17/1024	2.8
	29/1/2021	1525	Fine	0	0	0	20.9	18/1021	2.8
P17A	29/1/2021	1045	Fine	0	0	0	20.9	17/1024	5
	29/1/2021	1545	Fine	0	0	0	20.9	18/1021	5
P17B	29/1/2021	1055	Fine	0	0	0	20.9	17/1024	8
	29/1/2021	1555	Fine	0	0	0	20.9	18/1021	8
								/	
								/	
								/	
								/	

Name & Designation      Signature      Date  
 Field Operator:      Ting Wai Kin (Safety Officer [RencPipe])           29/1/2021  
 Laboratory Staff:  
 Checked by:

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
Area A	30-1-2021	0830	Fine	0	0	0	20.9	14 / 1024	4.2
	30-1-2021	1330	Fine	0	0	0	20.9	13 / 1022	4.2
	30-1-2021	1700	Fine	0	0	0	20.9	17 / 1021	4.2
Area B	30-1-2021	0845	Fine	0	0	0	20.9	14 / 1024	2.5
	30-1-2021	1345	Fine	0	0	0	20.9	18 / 1022	2.5
	30-1-2021	1645	Fine	0	0	0	20.9	17 / 1021	2.5

	Name & Designation	Signature	Date
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		30-1-2021
Laboratory Staff:			
Checked by:	C. F. Lam (Foreman)		30-1-2021

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used: PGM-2500 (GRAE III)	Dates calibrated 28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
CHFC 4357	30/1/2021	0835	Fine	0	0	0	20.9	15/1024	2.5
	30/1/2021	1357	Fine	0	0	0	20.9	18/1021	2.5
CHFC 0490	30/1/2021	0900	Fine	0	0	0	20.9	15/1024	2.5
	30/1/2021	1410	Fine	0	0	0	20.9	18/1021	2.5
P17C	30/1/2021	0915	Fine	0	0	0	20.9	15/1024	8
	30/1/2021	1415	Fine	0	0	0	20.9	18/1021	8
15/CHC2A66	30/1/2021	0905	Fine	0	0	0	20.9	15/1024	7.1
	30/1/2021	1435	Fine	0	0	0	20.9	18/1021	7.1
15/ P17C	30/1/2021	0945	Fine	0	0	0	20.9	16/1024	2.2
	30/1/2021	1445	Fine	0	0	0	20.9	18/1021	2.2
15/ P17B	30/1/2021	0955	Fine	0	0	0	20.9	16/1024	8.6
	30/1/2021	1505	Fine	0	0	0	20.9	18/1021	8.6
15/ P17A	30/1/2021	1005	Fine	0	0	0	20.9	16/1024	8.3
	30/1/2021	1505	Fine	0	0	0	20.9	18/1021	8.3

	<u>Name &amp; Designation</u>	<u>Signature</u>	<u>Date</u>
Field Operator:	Ting Wai Kin (Safety Officer [RenoPipe])		30/1/2021
Laboratory Staff:			
Checked by:			

ENVIRONMENTAL RESOURCES MANAGEMENT

ENVIRONMENTAL PROTECTION DEPARTMENT

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**




Contract no. 13/WSD/16  
 Mainlaying in Tseung Kwan O  
 Penta-Ocean - Concentric Joint Venture  
**Landfill Gas Monitoring –Field Measurement Recording Sheet**

Name of site: 13/WSD/16 - Mainlaying in Tseung Kwan O  
 Date of measurement:

Sampling equipment used:	Dates calibrated
PGM-2500 (QRAE III)	28 Jul 2020

Sample location	Date of measurement	Sampling time	Monitoring wells / Surface Gas Emission						
			Weather condition	Balance gas (%)	Flammable gas (methane %)	Carbon monoxide(%)	Oxygen (%)	Temp (°C) / Pressure (mbar)	Remark Depth (m)
WKE1	30/1/2021	1517	Fine	0	0	0	20.9	17/1024	2.2
	30/1/2021	1517	Fine	0	0	0	20.9	18/1021	2.2
CHASHT0	30/1/2021	1625	Fine	0	0	0	20.9	17/1024	2.8
	30/1/2021	1525	Fine	0	0	0	20.9	18/1021	2.8
P1A	30/1/2021	1047	Fine	0	0	0	20.9	17/1024	5
	30/1/2021	1527	Fine	0	0	0	20.9	18/1021	5
P1B	30/1/2021	1025	Fine	0	0	0	20.9	17/1024	8
	30/1/2021	1375	Fine	0	0	0	20.9	18/1021	8

Name & Designation                      Signature                      Date

Field Operator:                      Ting Wai Kin (Safety Officer [RencPipe])                                            30/1/2021

Laboratory Staff:

Checked by:

# Appendix K

## Complaint Log and Regulatory Compliance Proforma

**Statistical Summary of Environmental Complaints**

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
01 January 2021 - 31 January 2021	0	2	N/A

**Statistical Summary of Environmental Summons**

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Details
01 January 2021 - 31 January 2021	0	0	N/A

**Statistical Summary of Environmental Prosecution**

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Details
01 January 2021 - 31 January 2021	0	0	N/A

# Appendix L

# Site Inspection Proforma



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

**WEEKLY ENVIRONMENTAL INSPECTION CHECKLIST**

Inspection Date: 26/01/2021 Inspected by: ET: Charlotte Lau WSD: Law Sai Helen  
 Inspection Time: 9:30 - 11:30 Contractor: Geo King ISC: N/A

Weather						
Condition	<input checked="" type="checkbox"/> Sunny	<input type="checkbox"/> Fine	<input type="checkbox"/> Overcast	<input type="checkbox"/> Drizzle	<input type="checkbox"/> Rain	<input type="checkbox"/> Storm <input type="checkbox"/> Hazy
Temperature	<u>17</u> °C		Humidity	<input type="checkbox"/> High	<input checked="" type="checkbox"/> Moderate	<input type="checkbox"/> Low
Wind	<input checked="" type="checkbox"/> Calm	<input type="checkbox"/> Light	<input type="checkbox"/> Breeze	<input type="checkbox"/> Strong		

		N/A	Yes	No	Photo/Remarks
<b>0.00</b>	<b>General</b>				
0.01	Is the current Environmental Permit displayed conspicuously at all vehicle site entrances/exits for public's information at any time?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>Obs (3)</u>
0.02	Is ET Leader's log-book kept readily available for inspections?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>1.00</b>	<b>Construction Dust</b>				
1.01	Are dusty materials, such as excavated materials, building debris and construction materials, and exposed earth surface properly covered to prevent dust emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.02	Are screenings, enclosures, water spraying or vacuum cleaning devices provided to dusty construction works for dust suppression?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>Screening</u>
1.03	Are fumes or smoke emitting plants or construction activities shielded by a screen?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>No construction activities observed with fume/smoke</u>
1.04	Are wheel-washing facilities with high-pressure water jets provided at all site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Is wheel-washing provided to all vehicles leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are road section near the site exit free from dusty material?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>Reminder (2)</u>
1.07	Are all main haul roads inside the site paved or sprayed with water to minimize dust emission during vehicle movement?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>paved</u>
1.08	Are water spraying provided immediately prior to any loading or transfer of dusty materials?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.09	Are covers provided to all dump trucks carrying dusty materials when entering and leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>No dump truck observed</u>
1.10	Are the working areas for uprooting of trees, shrubs, or vegetation or the removal of boulders, poles, pillars sprayed with water to maintain the entire surface wet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Is exposed earth properly treated within six months after the last construction activity on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.12	Does the operation of plants on site free from dark smoke emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>✓ No MM (1/2)</u>

26/01





**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
1.13	Are vehicles travelling at speed not exceeding 15km/hr within the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.14	Are stock of more than 20 bags of cement or dry PFA covered or sheltered on top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15	Are de-bagging, batching and mixing processes of bagged cement carried out in sheltered areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are hoarding of at least 2.4m high provided along the site boundary adjoining areas accessible by the public?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Is open burning prohibited?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>2.00</b>	<b>Construction Noise (Airborne)</b>				
2.01	Are quiet plants adopted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ Noise label
2.02	Are the PMFs operating on site well-maintained to minimize the generation of excessive noise?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ regular inspection.
2.03	Are plants throttled down or turned off when not in use?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.04	Are the plants known to emit noise strongly in one direction oriented to face away from NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	↳ no nearby NSRs
2.05	Are moveable barriers provided to screen NSRs from plant or noisy operations?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	↳ none
2.06	Are silencers, mufflers and enclosures provided to plants?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Are the hoods, cover panels and inspection hatches of PMFs closed during operation?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	no operation of PMF observed.
2.08	Are purposely-built site hoarding construction with appropriate materials provided along the site boundary?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Are noisy operation properly scheduled to minimize exposure and cumulative impacts to nearby sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are valid noise emission label(s) affixed to all hand-held breakers operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Are valid noise emission label(s) affixed to all air compressors operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are all construction noise permit(s) applied for percussive piling work?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are construction noise permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are valid construction noise permit(s) displayed at all vehicular exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>3.00</b>	<b>Water Quality</b>				
3.01	Is effluent discharge license obtained for wastewater discharge from site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.02	Is effluent discharged according to the effluent discharge license?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	↳ no water discharge.
3.03	Is wastewater discharge from site properly treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

06/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 T: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
3.04	Are perimeter channels provided to intercept storm runoff from outside the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	obs (4)
3.05	Are sand/silt removal facilities such as sand/silt traps and sediment basins provided to remove sand/silt particles from runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.06	Is surface runoff diverted to sedimentation facilities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.07	Is the drainage system properly maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	obs (1)
3.08	Are construction works carefully programmed to minimize soil excavation works during rainy seasons?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.09	Are exposed soil surface protected by paving as soon as possible to reduce the potential of soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Are temporary access roads protected by crushed gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.11	Are exposed slope surface properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Is trench excavation avoided in the wet season as far as practicable, or if necessary, backfilled in short sections after excavation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.13	Are open stockpiles of construction materials on site covered by tarpaulin or similar fabric during construction?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.14	Is runoff from wheel-washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.15	Is oil leakage or spillage prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ drip tray
3.16	Are there any measures to prevent the release of oil and grease into the storm drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	↑ grease (2)
3.17	Are the oil interceptors/ grease traps properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.18	Are debris and rubbish generated on site collected, handled and disposed of properly to avoid them entering the streams?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.19	Are all fuel tanks and storage areas provided with locks and be sited on sealed areas, within bunds of capacity equal to 110% of the storage capacity of the largest tank?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.20	Are tanks, containers, storage area bunded and the locations locked as far as possible from the sensitive watercourse and stormwater drains?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.21	Are sufficient chemical toilets provided on site to handle sewage from construction work force?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.22	Are sewage disposal and toilet maintenance of the portable chemical toilets provided by the licensed contractors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.23	Is concrete washing water properly collected and treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>4.00</b>	<b>Waste Management</b>				
4.01	Is a trip-ticket system implemented to monitor the disposal of C&D and solid wastes at public filling facilities and landfills?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

06/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
4.02	Is a recording system implemented to record the amount of wastes generated, recycled and disposed of?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.03	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.04	Are chemical waste separated from other waste and collected by a licensed chemical waste collector?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Are trip tickets for chemical waste disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Is chemical waste reused and recycled on site as far as practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are all containers for chemical waste properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.08	Is chemical waste storage area used solely for storage of chemical waste and properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.09	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Is the chemical waste storage area enclosed on at least 3 sides and adequately ventilated?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.11	Is an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or of 20% by volume of the chemical waste stored in that area, whichever is the greatest, provide?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Are a routine cleaning and maintenance programme implemented for drainage systems, sump pits, and oil interceptors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Are sufficient general refuse disposal/collection points provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.15	Are appropriate measures adopted to minimize windblown litter and dust during transportation of waste?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.16	Are individual collectors for aluminum cans, plastic bottles and packaging material and office paper provided to encourage waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.17	Are C&D wastes sorted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.18	Are C&D waste disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.19	Are unused C&D materials or chemicals recycled or reused to reduce the quantity of waste?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are public fill and C&D waste reuse on site as far as practicable to avoid disposal off-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.21	Are the construction materials stored properly to minimize the potential for damage or contamination?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.22	Is a dumping license obtained to deliver public fill to public filling areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

06/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
<b>5.00</b>	<b>Landscape and Visual</b>				
5.01	Are Is site hoarding provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Are vegetation disturbance minimized or soil protected to reduce potential soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.03	Is construction light oriented away from the sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is grass hydroseeding provided to slopes as soon as the completion of works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Are damages to trees outside site boundary due construction works avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.06	Is excavation works carried out manually instead of machinery operation within 2.5m vicinity of any preserved trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.07	Are the retained and transplanted tree(s) properly protected and in good conditions?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.08	Are surgery works carried out for damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>6.00</b>	<b>Ecology</b>				
6.01	Is site runoff properly treated to prevent any silty runoff??	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>No water discharge.</i>
6.02	Are silt trap installed and well-maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.03	Are stockpiles properly covered to avoid generating silty runoff??	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.04	Are construction works restricted to works area which are clearly defined?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>7.00</b>	<b>Overall</b>				
7.01	Is the EM&A properly implemented in general?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

06/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 T: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

Remark / Follow up of Observation(s) and Non-compliance(s) of Last Weekly Site Inspection:

Pit D → J. Pit C → 5+90 → 12+50 → Pit B




Observation(s)

- (1) Gully was not properly covered with geo-textile and sandbags at low sides at Pit D, 5+90
- (2) Chemical spillage was found at ~~the~~ CHA 5+90.
- (3) Environmental permit was not observed at vehicle exit/entrance at 5+90.
- (4) Construction bunding was not enclosed fully at Pit B

Reminder(s)

- (1) Housekeeping was reminded at J. pit C
- (2) Debris at site entrance/exit ~~was~~ should be cleared at 5+90.
- (3) construction materials should not be placed at the planter rack at 5+90.

Signatures:

ET Representative	Contractor's Representative	WSD's Representative	IEC's Representative
			N/A
(Name: Cherie Leung)	(Name: Sam Ng)	(Name: Lawson Kwok)	(Name: N/A)

06/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

**WEEKLY ENVIRONMENTAL INSPECTION CHECKLIST**

Inspection Date: 15/01/2021 Inspected by: ET: Chorlene Lai WSD: Teddy Lin Fai  
 Contractor: Bruce Lam IEC: N/A  
 Inspection Time: 14:20-17:00

Weather:

Condition  Sunny  Fine  Overcast  Drizzle  Rain  Storm  Hazy

Temperature 19 °C Humidity  High  Moderate  Low

Wind  Calm  Light  Breeze  Strong

		N/A	Yes	No	Photo/Remarks
0.00	General				
0.01	Is the current Environmental Permit displayed conspicuously at all vehicle site entrances/exits for public's information at any time?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>Obs'ing</u>
0.02	Is ET Leader's log-book kept readily available for inspections?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.00	Construction Dust				
1.01	Are dusty materials, such as excavated materials, building debris and construction materials, and exposed earth surface properly covered to prevent dust emission?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>dusty materials were kept wet and covered</u>
1.02	Are screenings, enclosures, water spraying or vacuum cleaning devices provided to dusty construction works for dust suppression?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>dusty materials were kept wet and covered</u>
1.03	Are fumes or smoke emitting plants or construction activities shielded by a screen?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>No smoke from activities</u>
1.04	Are wheel-washing facilities with high-pressure water jets provided at all site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Is wheel-washing provided to all vehicles leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are road section near the site exit free from dusty material?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.07	Are all main haul roads inside the site paved or sprayed with water to minimize dust emission during vehicle movement?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>paved</u>
1.08	Are water spraying provided immediately prior to any loading or transfer of dusty materials?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.09	Are covers provided to all dump trucks carrying dusty materials when entering and leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>W/ down trucks covered</u>
1.10	Are the working areas for uprooting of trees, shrubs, or vegetation or the removal of boulders, poles, pillars sprayed with water to maintain the entire surface wet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Is exposed earth properly treated within six months after the last construction activity on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.12	Does the operation of plants on site free from dark smoke emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>1/DIRMM</u>

15/1



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
1.13	Are vehicles travelling at speed not exceeding 15km/hr within the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.14	Are stock of more than 20 bags of cement or day PFA covered or sheltered on top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15	Are dc-bagging, batching and mixing processes of bagged cement carried out in sheltered areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are hoarding of at least 2.4m high provided along the site boundary adjoining areas accessible by the public?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Is open burning prohibited?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.00	<b>Construction Noise (Airborne)</b>				
2.01	Are quiet plants adopted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ARME
2.02	Are the PME's operating on site well-maintained to minimize the generation of excessive noise?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓regular inspection
2.03	Are plants throttled down or turned off when not in use?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.04	Are the plants known to emit noise strongly in one direction oriented to face away from NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓no nearby noise
2.05	Are moveable barriers provided to screen NSRs from plant or noisy operations?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓
2.06	Are silencers, mufflers and enclosures provided to plants?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Are the hoods, cover panels and inspection hatches of PME's closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.08	Are purposely-built site hoarding construction with appropriate materials provided along the site boundary?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Are noisy operation properly scheduled to minimize exposure and cumulative impacts to nearby sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are valid noise emission label(s) affixed to all hand-held breakers operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Are valid noise emission label(s) affixed to all air compressors operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are all construction noise permit(s) applied for percussive piling work?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are construction noise permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are valid construction noise permit(s) displayed at all vehicular exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.00	<b>Water Quality</b>				
3.01	Is effluent discharge license obtained for wastewater discharge from site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.02	Is effluent discharged according to the effluent discharge license?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓no effluent discharge observed
3.03	Is wastewater discharge from site properly treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓

1511



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
3.04	Are perimeter channels provided to intercept storm runoff from outside the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.05	Are sand/silt removal facilities such as sand/silt traps and sediment basins provided to remove sand/silt particles from runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.06	Is surface runoff diverted to sedimentation facilities?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.07	Is the drainage system properly maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	obscure
3.08	Are construction works carefully programmed to minimize soil excavation works during rainy seasons?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.09	Are exposed soil surface protected by paving as soon as possible to reduce the potential of soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Are temporary access roads protected by crushed gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.11	Are exposed slope surface properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Is trench excavation avoided in the wet season as far as practicable, or if necessary, backfilled in short sections after excavation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.13	Are open stockpiles of construction materials on site covered by tarpaulin or similar fabric during construction?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.14	Is runoff from wheel-washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.15	Is oil leakage or spillage prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.16	Are there any measures to prevent the release of oil and grease into the storm drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.17	Are the oil interceptors/ grease traps properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.18	Are debris and rubbish generated on site collected, handled and disposed of properly to avoid them entering the streams?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.19	Are all fuel tanks and storage areas provided with locks and be sited on sealed areas, within bunds of capacity equal to 110% of the storage capacity of the largest tank?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.20	Are tanks, containers, storage area bunded and the locations locked as far as possible from the sensitive watercourse and stormwater drains?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.21	Are sufficient chemical toilets provided on site to handle sewage from construction work force?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.22	Are sewage disposal and toilet maintenance of the portable chemical toilets provided by the licensed contractors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.23	Is concrete washing water properly collected and treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>4.00</b>	<b>Waste Management</b>				
4.01	Is a trip-ticket system implemented to monitor the disposal of C&D and solid wastes at public filling facilities and landfills?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

15/1





**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
4.02	Is a recording system implemented to record the amount of wastes generated, recycled and disposed of?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.03	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.04	Are chemical waste separated from other waste and collected by a licensed chemical waste collector?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Are trip tickets for chemical waste disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Is chemical waste reused and recycled on site as far as practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are all containers for chemical waste properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.08	Is chemical waste storage area used solely for storage of chemical waste and properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.09	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Is the chemical waste storage area enclosed on at least 3 sides and adequately ventilated?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.11	Is an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or of 20% by volume of the chemical waste stored in that area, whichever is the greatest, provide?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Are a routine cleaning and maintenance programme implemented for drainage systems, sump pits, and oil interceptors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Are sufficient general refuse disposal/collection points provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.15	Are appropriate measures adopted to minimize windblown litter and dust during transportation of waste?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.16	Are individual collectors for aluminum cans, plastic bottles and packaging material and office paper provided to encourage waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.17	Are C&D wastes sorted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.18	Are C&D waste disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.19	Are unused C&D materials or chemicals recycled or reused to reduce the quantity of waste?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are public fill and C&D waste reuse on site as far as practicable to avoid disposal off-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.21	Are the construction materials stored properly to minimize the potential for damage or contamination?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.22	Is a dumping license obtained to deliver public fill to public filling areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

15/1



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
<b>5.00</b>	<b>Landscape and Visual</b>				
5.01	Are Is site hoarding provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Are vegetation disturbance minimized or soil protected to reduce potential soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.03	Is construction light oriented away from the sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is grass hydroseeding provided to slopes as soon as the completion of works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Are damages to trees outside site boundary due construction works avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.06	Is excavation works carried out manually instead of machinery operation within 2.5m vicinity of any preserved trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.07	Are the retained and transplanted tree(s) properly protected and in good conditions?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.08	Are surgery works carried out for damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>6.00</b>	<b>Ecology</b>				
6.01	Is site runoff properly treated to prevent any silty runoff?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<i>no water discharge</i>
6.02	Are silt trap installed and well-maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.03	Are stockpiles properly covered to avoid generating silty runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.04	Are construction works restricted to works area which are clearly defined?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>7.00</b>	<b>Overall</b>				
7.01	Is the EM&A properly implemented in general?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

(5/1)



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

Remark / Follow up of Observation(s) and Non-compliance(s) of Last Weekly Site Inspection:

WPR1, 2 → ~~3+62~~ → 7+42.




Observation (S) 3+62 7+42.

(1) Environmental permit was not observed at the vehicle entrance/exit at WPR1, 2, 3+62

(2) ~~Quality~~ Gutters were not properly protected by sandbags and geotextile at WPR2, 3+62, 7+42.

---

Signatures:

ET Representative	Contractor's Representative	WSD's Representative	IEC's Representative
			N/A
(Name: <i>charlene lai</i> )	(Name: <i>Bruce Lam</i> )	(Name: <i>Shing Kin Fong</i> )	(Name: N/A)

(51)



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

**WEEKLY ENVIRONMENTAL INSPECTION CHECKLIST**

Inspection Date: 21/01/2021 Inspected by: ET: Charlotte Lai WSD: C.K. Cheng  
 Contractor: Lan Tai Ltd IEC: N/A  
 Inspection Time: 09:30-11:30

Weather							
Condition	<input type="checkbox"/> Sunny	<input type="checkbox"/> Fine	<input type="checkbox"/> Overcast	<input type="checkbox"/> Drizzle	<input type="checkbox"/> Rain	<input type="checkbox"/> Storm	<input type="checkbox"/> Hazy
Temperature	<input type="text"/> C		Humidity	<input type="checkbox"/> High	<input type="checkbox"/> Moderate	<input type="checkbox"/> Low	
Wind	<input type="checkbox"/> Calm	<input type="checkbox"/> Light	<input type="checkbox"/> Breeze	<input type="checkbox"/> Strong			

		N/A	Yes	No	Photo/Remarks
<b>0.00</b>	<b>General</b>				
0.01	Is the current Environmental Permit displayed conspicuously at all vehicle site entrances/exits for public's information at any time?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>ok(s)</u>
0.02	Is ET Leader's log-book kept readily available for inspections?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>1.00</b>	<b>Construction Dust</b>				
1.01	Are dusty materials, such as excavated materials, building debris and construction materials, and exposed earth surface properly covered to prevent dust emission?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>water spraying</u>
1.02	Are screenings, enclosures, water spraying or vacuum cleaning devices provided to dusty construction works for dust suppression?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>water spraying</u>
1.03	Are fumes or smoke emitting plants or construction activities shielded by a screen?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.04	Are wheel-washing facilities with high-pressure water jets provided at all site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Is wheel-washing provided to all vehicles leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are roof section near the site exit free from dusty material?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.07	Are all main haul roads inside the site paved or sprayed with water to minimize dust emission during vehicle movement?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>paved.</u>
1.08	Are water spraying provided immediately prior to any loading or transfer of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.09	Are covers provided to all dump trucks carrying dusty materials when entering and leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>no dump trucks observed</u>
1.10	Are the working areas for uprooting of trees, shrubs, or vegetation or the removal of boulders, poles, pillars sprayed with water to maintain the entire surface wet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Is exposed earth properly treated within six months after the last construction activity on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.12	Does the operation of plants on site free from dark smoke emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<u>N/A with label</u>

21/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
1.13	Are vehicles travelling at speed not exceeding 15km/hr within the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.14	Are stock of more than 20 bags of cement or day PFA covered or sheltered on top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15	Are de-bagging, batching and mixing processes of bagged cement carried out in sheltered areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are hoarding of at least 2.4m high provided along the site boundary adjoining areas accessible by the public?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Is open burning prohibited?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>2.00</b>	<b>Construction Noise (Airborne)</b>				
2.01	Are quiet plants adopted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ at ME 10/11
2.02	Are the PME's operating on site well-maintained to minimize the generation of excessive noise?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.03	Are plants throttled down or turned off when not in use?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.04	Are the plants known to emit noise strongly in one direction oriented to face away from NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓ no nearby NSR
2.05	Are moveable barriers provided to screen NSRs from plant or noisy operations?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓
2.06	Are silencers, mufflers and enclosures provided to plants?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Are the hoods, cover panels and inspection hatches of PMEs closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.08	Are purposely-built site hoarding construction with appropriate materials provided along the site boundary?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Are noisy operation properly scheduled to minimize exposure and cumulative impacts to nearby sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are valid noise emission label(s) affixed to all hand-held breakers operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Are valid noise emission label(s) affixed to all air compressors operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are all construction noise permit(s) applied for percussive piling work?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are construction noise permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are valid construction noise permit(s) displayed at all vehicular exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>3.00</b>	<b>Water Quality</b>				
3.01	Is effluent discharge license obtained for wastewater discharge from site?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.02	Is effluent discharged according to the effluent discharge license?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓
3.03	Is wastewater discharge from site properly treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓ water discharge on the property def.

2/10/1



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333 1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
3.04	Are perimeter channels provided to intercept storm runoff from outside the site?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Obs (1)
3.05	Are sand/silt removal facilities such as sand/silt traps and sediment basins provided to remove sand/silt particles from runoff?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Yes now photo change
3.06	Is surface runoff diverted to sedimentation facilities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.07	Is the drainage system properly maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Obs (2)
3.08	Are construction works carefully programmed to minimize soil excavation works during rainy seasons?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.09	Are exposed soil surface protected by paving as soon as possible to reduce the potential of soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Are temporary access roads protected by crushed gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.11	Are exposed slope surface properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Is trench excavation avoided in the wet season as far as practicable, or if necessary, backfilled in short sections after excavation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.13	Are open stockpiles of construction materials on site covered by tarpaulin or similar fabric during construction?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.14	Is runoff from wheel-washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.15	Is oil leakage or spillage prevented?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Obs (4)
3.16	Are there any measures to prevent the release of oil and grease into the storm drainage system?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Obs (4)
3.17	Are the oil interceptors/ grease traps properly maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Obs (4)
3.18	Are debris and rubbish generated on site collected, handled and disposed of properly to avoid them entering the streams?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.19	Are all fuel tanks and storage areas provided with locks and be sited on sealed areas, within bunds of capacity equal to 110% of the storage capacity of the largest tank?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.20	Are tanks, containers, storage area banded and the locations locked as far as possible from the sensitive watercourse and stormwater drains?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.21	Are sufficient chemical toilets provided on site to handle sewage from construction work force?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.22	Are sewage disposal and toilet maintenance of the portable chemical toilets provided by the licensed contractors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.23	Is concrete washing water properly collected and treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>4.00</b>	<b>Waste Management</b>				
4.01	Is a trip-ticket system implemented to monitor the disposal of C&D and solid wastes at public filling facilities and landfills?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

21/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 T: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
4.02	Is a recording system implemented to record the amount of wastes generated, recycled and disposed of?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.03	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.04	Are chemical waste separated from other waste and collected by a licensed chemical waste collector?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Are trip tickets for chemical waste disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Is chemical waste reused and recycled on site as far as practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are all containers for chemical waste properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.08	Is chemical waste storage area used solely for storage of chemical waste and properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.09	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Is the chemical waste storage area enclosed on at least 3 sides and adequately ventilated?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.11	Is an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or of 20% by volume of the chemical waste stored in that area, whichever is the greatest, provide?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Are a routine cleaning and maintenance programme implemented for drainage systems, sump pits, and oil interceptors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Are sufficient general refuse disposal/collection points provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.15	Are appropriate measures adopted to minimize windblown litter and dust during transportation of waste?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.16	Are individual collectors for aluminum cans, plastic bottles and packaging material and office paper provided to encourage waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.17	Are C&D wastes sorted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.18	Are C&D waste disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.19	Are unused C&D materials or chemicals recycled or reused to reduce the quantity of waste?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are public fill and C&D waste reuse on site as far as practicable to avoid disposal off-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.21	Are the construction materials stored properly to minimize the potential for damage or contamination?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.22	Is a dumping license obtained to deliver public fill to public filling areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

21/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333 6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
<b>5.00</b>	<b>Landscape and Visual</b>				
5.01	Are Is site hoarding provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Are vegetation disturbance minimized or soil protected to reduce potential soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.03	Is construction light oriented away from the sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is grass hydrosceding provided to slopes as soon as the completion of works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Are damages to trees outside site boundary due construction works avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	remover (1)
5.06	Is excavation works carried out manually instead of machinery operation within 2.5m vicinity of any preserved trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.07	Are the retained and transplanted tree(s) properly protected and in good conditions?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.08	Are surgery works carried out for damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>6.00</b>	<b>Ecology</b>				
6.01	Is site runoff properly treated to prevent any silty runoff?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	no water discharge
6.02	Are silt trap installed and well-maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.03	Are stockpiles properly covered to avoid generating silty runoff?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓ water spraying
6.04	Are construction works restricted to works area which are clearly defined?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>7.00</b>	<b>Overall</b>				
7.01	Is the EM&A properly implemented in general?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

211





**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com


**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

Remark / Follow up of Observation(s) and Non-compliance(s) of Last Weekly Site Inspection:

Pit D → Pit C → 137 Pit B → 137 Pit A → Pit 137 C → WPK1 → WPK2 → Main W4  
 T207

Observation(s)

- (1) construction boundaries were not fully protected by sandbags.
- (2) Environmental permit was not observed at the exit/entrance.
- (3) Gully was not protected by sandbags & geo-textile mat at WPK1.
- (4) Chemicals were not placed inside a drip tray at WPK1.



Reminders

- (1) The Main Contractor was reminded to implement measures to protect tree roots around the site boundary.

**Signatures:**

ET  
Representative

Contractor's  
Representative

WSD's  
Representative

IFC's  
Representative









(Name: Chondencat)

(Name: Lam Tsz Ho)

(Name: F.K. Cheung)

(Name: N/A)

21/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

**WEEKLY ENVIRONMENTAL INSPECTION CHECKLIST**

Inspection Date: 25/01/2021 Inspected by: ET: Charlene Law WSD: Low Sai Kuen  
 Inspection Time: 09:30 - 12:00 Contractor: Sammoy IFC: Resource Group (Lau Kwan)

Weather	
Condition	<input checked="" type="checkbox"/> Sunny <input type="checkbox"/> Fine <input type="checkbox"/> Overcast <input type="checkbox"/> Drizzle <input type="checkbox"/> Rain <input type="checkbox"/> Storm <input type="checkbox"/> Heavy
Temperature	<input type="checkbox"/> 20 C <input type="checkbox"/> Humidity <input type="checkbox"/> High <input checked="" type="checkbox"/> Moderate <input type="checkbox"/> Low
Wind	<input checked="" type="checkbox"/> Calm <input type="checkbox"/> Light <input type="checkbox"/> Breeze <input type="checkbox"/> Strong

		N/A	Yes	No	Photo/Remarks
<b>0.00</b>	<b>General</b>				
0.01	Is the current Environmental Permit displayed conspicuously at all vehicle site entrances/exits for public's information at any time?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
0.02	Is ET Leader's log-book kept readily available for inspections?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>1.00</b>	<b>Construction Dust</b>				
1.01	Are dusty materials, such as excavated materials, building debris and construction materials, and exposed earth surface properly covered to prevent dust emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.02	Are screenings, enclosures, water spraying or vacuum cleaning devices provided to dusty construction works for dust suppression?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	screening, watering
1.03	Are fumes or smoke emitting plants or construction activities shielded by a screen?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.04	Are wheel-washing facilities with high-pressure water jets provided at all site exits?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.05	Is wheel-washing provided to all vehicles leaving the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.06	Are road section near the site exit free from dusty material?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.07	Are all main haul roads inside the site paved or sprayed with water to minimize dust emission during vehicle movement?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	paved
1.08	Are water spraying provided immediately prior to any loading or transfer of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.09	Are covers provided to all dump trucks carrying dusty materials when entering and leaving the site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	No dump truck observed
1.10	Are the working areas for uprooting of trees, shrubs, or vegetation or the removal of boulders, poles, pillars sprayed with water to maintain the entire surface wet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Is exposed earth properly treated within six months after the last construction activity on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.12	Does the operation of plants on site free from dark smoke emission?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ ARRIVED later

25/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
1.13	Are vehicles travelling at speed not exceeding 15km/hr within the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.14	Are stock of more than 20 bags of cement or day PFA covered or sheltered on top and 3 sides?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.15	Are de-bagging, batching and mixing processes of bagged cement carried out in sheltered areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are hoarding of at least 2.4m high provided along the site boundary adjoining areas accessible by the public?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Is open burning prohibited?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>2.00</b>	<b>Construction Noise (Airborne)</b>				
2.01	Are quiet plants adopted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ noise level
2.02	Are the PMEs operating on site well-maintained to minimize the generation of excessive noise?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	✓ regular inspection
2.03	Are plants throttled down or turned off when not in use?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.04	Are the plants known to emit noise strongly in one direction oriented to face away from NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓ away from NSR
2.05	Are moveable barriers provided to screen NSRs from plant or noisy operations?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	✓
2.06	Are silencers, mufflers and enclosures provided to plants?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Are the hoods, cover panels and inspection hatches of PMEs closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.08	Are purposely-built site hoarding construction with appropriate materials provided along the site boundary?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Are noisy operation properly scheduled to minimize exposure and cumulative impacts to nearby sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are valid noise emission label(s) affixed to all hand-held breakers operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Are valid noise emission label(s) affixed to all air compressors operating on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are all construction noise permit(s) applied for percussive piling work?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are construction noise permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are valid construction noise permit(s) displayed at all vehicular exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>3.00</b>	<b>Water Quality</b>				
3.01	Is effluent discharge license obtained for wastewater discharge from site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.02	Is effluent discharged according to the effluent discharge license?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	EMS C12
3.03	Is wastewater discharge from site properly treated prior to discharge?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	MSD

25/1



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 Q: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
3.04	Are perimeter channels provided to intercept storm runoff from outside the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.05	Are sand/silt removal facilities such as sand/silt traps and sediment basins provided to remove sand/silt particles from runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.06	Is surface runoff diverted to sedimentation facilities?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.07	Is the drainage system properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.08	Are construction works carefully programmed to minimize soil excavation works during rainy seasons?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.09	Are exposed soil surface protected by paving as soon as possible to reduce the potential of soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Are temporary access roads protected by crushed gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.11	Are exposed slope surface properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Is trench excavation avoided in the wet season as far as practicable, or if necessary, backfilled in short sections after excavation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.13	Are open stockpiles of construction materials on site covered by tarpaulin or similar fabric during construction?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.14	Is runoff from wheel-washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.15	Is oil leakage or spillage prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	obs (2)
3.16	Are there any measures to prevent the release of oil and grease into the storm drainage system?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	obs (2)
3.17	Are the oil interceptors/ grease traps properly maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.18	Are debris and rubbish generated on site collected, handled and disposed of properly to avoid them entering the streams?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.19	Are all fuel tanks and storage areas provided with locks and be sited on sealed areas, within bunds of capacity equal to 110% of the storage capacity of the largest tank?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.20	Are tanks, containers, storage area bunded and the locations locked as far as possible from the sensitive watercourse and stormwater drains?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.21	Are sufficient chemical toilets provided on site to handle sewage from construction work force?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.22	Are sewage disposal and toilet maintenance of the portable chemical toilets provided by the licensed contractors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.23	Is concrete washing water properly collected and treated prior to discharge?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>4.00</b>	<b>Waste Management</b>				
4.01	Is a trip-ticket system implemented to monitor the disposal of C&D and solid wastes at public filling facilities and landfills?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

25/11



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
4.02	Is a recording system implemented to record the amount of wastes generated, recycled and disposed of?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.03	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.04	Are chemical waste separated from other waste and collected by a licensed chemical waste collector?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Are trip tickets for chemical waste disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Is chemical waste reused and recycled on site as far as practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are all containers for chemical waste properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.08	Is chemical waste storage area used solely for storage of chemical waste and properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.09	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Is the chemical waste storage area enclosed on at least 3 sides and adequately ventilated?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.11	Is an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or of 20% by volume of the chemical waste stored in that area, whichever is the greatest, provide?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Are a routine cleaning and maintenance programme implemented for drainage systems, sump pits, and oil interceptors?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Are sufficient general refuse disposal/collection points provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	remainder (c)
4.15	Are appropriate measures adopted to minimize windblown litter and dust during transportation of waste?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.16	Are individual collectors for aluminium cans, plastic bottles and packaging material and office paper provided to encourage waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.17	Are C&D wastes sorted on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.18	Are C&D waste disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.19	Are unused C&D materials or chemicals recycled or reused to reduce the quantity of waste?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are public fill and C&D waste reuse on site as far as practicable to avoid disposal off-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	timber
4.21	Are the construction materials stored properly to minimize the potential for damage or contamination?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.22	Is a dumping license obtained to deliver public fill to public filling areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

25/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

		N/A	Yes	No	Photo/Remarks
<b>5.00</b>	<b>Landscape and Visual</b>				
5.01	Are site hoarding provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Are vegetation disturbance minimized or soil protected to reduce potential soil erosion?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.03	Is construction light oriented away from the sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is grass hydroseeding provided to slopes as soon as the completion of works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Are damages to trees outside site boundary due construction works avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	reminders
5.06	Is excavation works carried out manually instead of machinery operation within 2.5m vicinity of any preserved trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.07	Are the retained and transplanted tree(s) properly protected and in good conditions?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.08	Are surgery works carried out for damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<b>6.00</b>	<b>Ecology</b>				
6.01	Is site runoff properly treated to prevent any silty runoff?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Obs (1)
6.02	Are silt trap installed and well-maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6.03	Are stockpiles properly covered to avoid generating silty runoff?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.04	Are construction works restricted to works area which are clearly defined?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<b>7.00</b>	<b>Overall</b>				
7.01	Is the EM&A properly implemented in general?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

25/01



**Acuity Sustainability Consulting Limited**

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T.  
 O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com

**Contract no. 13/WSD/16 Mainlaying in Tseung Kwan O**

Remark / Follow up of Observation(s) and Non-compliance(s) of Last Weekly Site Inspection:

Observation(s) H.K. Velodrome

- (1) The desilting or water treatment facility was observed leaking. The contractor was reminded to replace a new water treatment facility to ensure proper treatment of wastewater before discharging at H.K. Velodrome.
- (2) Grab was not placed on top of a tarpaulin sheet which may lead to accidental contamination of the ground by chemical at H.K. Velodrome.

Reminders:

- (1) The contractor was reminded to clear up the debris near the construction site exit/entrance of H.K. Velodrome.
- (2) The contractor was reminded to extend the protection fence to the over the road at H.K. Velodrome.

**Signatures:**

ET Representative



(Name: *Christine Chan*)

Contractor's Representative



(Name: *Sam Ng*)

WSD's Representative



(Name: *Ann M. Leung*)  
(*AKELUO*)

IEC's Representative



(Name: *Louis Ng*)  
*Reasonable Cherry*

# Appendix M

## Proactive Environmental Protection Proforma



**Proactive Environmental Protection for the Next Reporting Month**

<b>Reporting Period</b>	<b>Activity</b>	<b>Major Environmental Impact</b>	<b>Environmental Mitigation Measure</b>
1 February 2021 - 28 February 2021	<ul style="list-style-type: none"> <li>- Excavation of trench</li> <li>- Mainlaying of pipe</li> <li>- Backfilling of the trench</li> <li>- Work fronts for open trench</li> <li>- Work fronts for pipe jacking</li> </ul>	Construction dust and noise generation; construction wastes	<ul style="list-style-type: none"> <li>- Dust suppression by regular wetting and water spraying</li> <li>- Reduction of noise from equipment and machinery on-site</li> <li>- Sorting and storage of general refuse and construction waste</li> </ul>

## Appendix N

# Impact Monitoring Schedule of Next Reporting Month (Tentative)

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.30**



Feb-21						
Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2	3 Noise Impact Monitoring	4	5	6
7	8 Noise Impact Monitoring	9	10	11	12	13
14	15	16	17	18	19 Noise Impact Monitoring	20
21	22 Noise Impact Monitoring	23	24	25	26	27
28						

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

# Appendix O

## Academic Calendar(s)

**Contract No. 13/WSD/16**  
**Mainlaying in Tseung Kwan O**  
**Monthly EM&A Report No.28**



CREATIVE SECONDARY SCHOOL CALENDAR 2020-2021									
Month	Day	Su	Mo	Tu	We	Th	Fr	Sa	
August	2								
		9	10	11	12	13	14	15	
		16	17	18	19	20	21	22	
		23	24A	25B	26C	27D	28E	29	
		30	31F						
								19/8 First School day	
September	2			1A	2B	3C	4D	5	
	3	6	7E	8F	9A	10B	11C	12	
		13	14D	15E	16F	17A	18B	19	
	4	20	21C	22D	23E	24F	25A	26	
	5	27	28B	29C	30				
								28/9 F1/MY1 3-Way Conference, 30/9 Staff Development Day 1	
October		4	5D	6E	7F	8A	9B	10	
	6	11	12C	13D	14E	15F	16A	17	
		18	19	20	21	22	23	24	
	7	25	26	27B	28C	29D	30E	31	
									26/10 Chung Yeung Festival Holiday.
	8	1	2F	3A	4B	5C	6D	7	
		8	9	10E	11F	12A	13B	14	
	9	15	16C	17D	18E	19F	20A	21	
	10	22	23B	24C	25D	26E	27F	28	
	11	29	30A						
November				1B	2C	3D	4E	5	
	12	6	7E	8F	9A	10B	11C	12	
		13	14D	15E	16F	17A	18B	19	
		20	21	22	23	24	25	26	
		27	28	29	30	31			
								15/12 F4 3-Way Conference	
								25/12 Christmas Day 16/12 The First Weekday after Christmas Day	
								21/12-2/1 Christmas & New Year Holiday	
January						1	2		
	13	3	4C	5D	6E	7F	8A	9	
	14	10	11B	12C	13D	14E	15F	16	
	15	17	18A	19B	20C	21D	22E	23	
	16	24	25F	26A	27B	28C	29D	30	
		31							
								1/1 New Year's Day	
February	17		1E	2F	3A	4B	5C	6	
		7	8D	9E	10	11	12	13	
		14	15	16	17	18	19	20	
	18	21	22F	23A	24B	25C	26D	27	
		28							
								12-15 New year Holiday. 10-20/2 Chinese New Year Holiday	
March	19		1E	2F	3A	4B	5C	6	
		7	8D	9E	10F	11A	12B	13	
	20	14	15C	16D	17E	18F	19A	20	
		21	22	23	24	25	26	27	
	21	28	29B	30C	31D				
								4/3 F2 3-Way Conference, 5/3 Last school day for F6 HKDSE students	
April						1	2	3	
		4	5	6	7	8	9	10	
	22	11	12E	13F	14A	15B	16C	17	
		18	19D	20E	21F	22A	23B	24	
	23	25	26C	27D	28E	29F	30A		
									01/04-10/04 Easter Holiday. 02/04 Good Friday, 03/04 The Day following Good Friday
								04/04 Ching Ming Festival. 05/04 Easter Monday, 9-19/4 F6 HKDSE Exams-CSS Hall	
								16/4 Last school day for F6 IBDP students	
May									
									27/4 F1/MY1 3-Way Conference 30/4-19/5 F6 IBDP May Exams
	24	2	3B	4C	5D	6E	7F	8	
	25	9	10A	11B	12C	13D	14E	15	
	26	16	17F	18A	19B	20C	21D	22	
	27	23	24D	25E	26F	27A	28B	29	
	30	31C							
								1/5 Labour Day	
								4-17/5 F5 HKDSE Final Exams	
June	24	2	3B	4C	5D	6E	7F	8	
	25	9	10A	11B	12C	13D	14E	15	
	26	16	17F	18A	19B	20C	21D	22	
	27	23	24D	25E	26F	27A	28B	29	
		30	31C						
								19/5 Birthday of Buddha, 21-27/5 F4 HKDSE Exams & F5 IBDP Final Exams	
July									
								01/07 Tuen Ng Festival	
August									
								01/07 HKSAR Establishment Day, 2/7-14/8 Summer Holiday	
August									

Sourced from:  
[https://1e833fb1-5af5-4de8-901f-f9aeda4354b2.filesusr.com/ugd/611a22\\_ea5d81f9881541de9c3c7049ba46860d.pdf](https://1e833fb1-5af5-4de8-901f-f9aeda4354b2.filesusr.com/ugd/611a22_ea5d81f9881541de9c3c7049ba46860d.pdf)

中華人民共和國香港特別行政區政府總部教育局

Education Bureau

Government Secretariat, The Government of the Hong Kong Special Administrative Region  
The People's Republic of China

本局檔號 Our Ref: EDB(SDCT)3/PRO/10/1/1

電話 Telephone:

來函檔號 Your Ref.:

傳真 Fax Line:

30 November 2020

To: Supervisors / Principals of All Secondary Schools, Primary Schools, Special Schools, Schools offering Non-Local Curriculum, Kindergartens and Kindergarten-cum-Child Care Centres and Private Schools offering Non-Formal Curriculum

Dear Supervisor / Principal,

**Arrangements of Suspension of Face-to-face Classes for All Schools**

Further to the Government's earlier separate announcements on suspension of face-to-face classes and school activities for all kindergartens and Primary 1 to Primary 3 levels of primary schools until December 6, the Government announced yesterday (29 November) that in light of the worsening situation of the COVID-19 epidemic, all kindergartens as well as primary and secondary schools (including special schools and schools offering non-local curriculum) would suspend face-to-face classes and school activities starting from 2 December (Wednesday) this year until the beginning of school Christmas holidays. Private schools offering non-formal curriculum (commonly known as "tutorial schools") will suspend face-to-face classes for all classes for two weeks until 15 December.

[https://www.edb.gov.hk/attachment/en/sch-admin/admin/about-sch/diseases-prevention/edb\\_20201130\\_eng.pdf](https://www.edb.gov.hk/attachment/en/sch-admin/admin/about-sch/diseases-prevention/edb_20201130_eng.pdf)



中華人民共和國香港特別行政區政府總部教育局

Education Bureau

Government Secretariat, The Government of the Hong Kong Special Administrative Region  
The People's Republic of China

本局檔號 Our Ref: EDB(SDCT)3/PRO/10/1/1

電話 Telephone:

來函檔號 Your Ref.:

傳真 Fax Line:

21 December 2020

To: Supervisors / Principals of All Secondary Schools, Primary Schools, Special Schools, Schools offering Non-Local Curriculum, Kindergartens and Kindergarten-cum-Child Care Centres and Private Schools offering Non-Formal Curriculum

Dear Supervisor / Principal,

**Arrangements of Further Suspension of Face-to-Face Classes for All Schools**

Since the situation of COVID-19 is still very severe, the Government needs to take stringent measures to cope with the epidemic. The Education Bureau (EDB) has announced that all kindergartens as well as primary and secondary schools (including special schools and schools offering non-local curriculum) will further suspend face-to-face classes and school activities after the end of the scheduled Christmas holidays until 10 January 2021. For private schools offering non-formal curriculum (commonly known as “tutorial schools”), face-to-face classes and school activities of all levels will also be suspended until 10 January 2021.

[https://www.edb.gov.hk/attachment/en/sch-admin/admin/about-sch/diseases-prevention/edb\\_20201221\\_eng.pdf](https://www.edb.gov.hk/attachment/en/sch-admin/admin/about-sch/diseases-prevention/edb_20201221_eng.pdf)



中華人民共和國香港特別行政區政府總部教育局  
Education Bureau  
Government Secretariat, The Government of the Hong Kong Special Administrative Region  
The People's Republic of China

本局檔號 Our Ref: EDB(SDCT)3/PRO/10/1/1

電話 Telephone:

來函檔號 Your Ref.:

傳真 Fax Line:

4 January 2021

To: Supervisors / Principals of All Secondary Schools, Primary Schools, Special Schools, Schools offering Non-Local Curriculum, Kindergartens and Kindergarten-Child Care Centres and Private Schools offering Non-Formal Curriculum

Dear Supervisor / Principal,

**Continuation of Suspension of Face-to-Face Classes for Schools in Hong Kong:  
The Arrangements**

Since the situation of COVID-19 is still severe, the Government has decided to maintain the existing social distancing measures until 20 January 2021. Schools will dovetail with the arrangements, and the Education Bureau (EDB) has decided that all kindergartens, primary and secondary schools (including special schools and schools offering non-local curriculum) as well as schools offering non-formal curriculum (PSNFCs) (commonly known as "tutorial schools") will continue the suspension of face-to-face classes and school activities after 10 January 2021. The suspension will continue until the beginning of schools' Chinese New Year holidays.

Sourced from:

[https://www.edb.gov.hk/attachment/en/sch-admin/admin/about-sch/diseases-prevention/edb\\_20210104\\_eng.pdf](https://www.edb.gov.hk/attachment/en/sch-admin/admin/about-sch/diseases-prevention/edb_20210104_eng.pdf)
