





Website: www.acuityhk.com



Unit C, 11/F, Ford Glory Plaza, Nos. 37-39 Wing Hong Street, Cheung Sha Wan, Kowloon.

C

Tel. : (852) 2698 6833 Fax.: (852) 2698 9383

Contract No. AL G513

Expansion of Wo Hop Shek Crematorium

Quarterly EM&A Report No.6 (Period from 1 July to 30 September 2021)

Document No.

ASCL	/	2018028	/	0006	/	A
Publisher		Project Code		Sequential No.		Revision
						Index

	Prepared by:	Reviewed by:	Certified by:
Name	Philip CHAN	Nelson TSUI	Kevin LI
Position	Environmental Team	Environmental Team	Environmental Team
Position	Member	Member	Leader
Signature	Philip		X;
Date:	08/10/2021	08/10/2021	08/10/2021



REVISION HISTORY

REV.	DESCRIPTION OF MODIFICATION	DATE
Α	First Issue for Comments	08 OCT 2021



CONTENTS

Executive Sumi	mary	1		
1. Basic Proje	ect Information	3		
2. Monitoring	g Results	10		
3. Waste		13		
	of Monitoring Exceedance, Complaints, Notification of Summons and Prosec			
	Inspection			
	ns and Recommendations			
Appendix A	Master Programme			
Appendix B	pendix B Work Area for the Contract No. AL G513			
Appendix C	Appendix C Summary of Implementation Status of Environmental Mitigation			
Appendix D	Impact Monitoring Schedule of the Reporting Period			
Appendix E	Event/Action Plan for Dust Exceedance			
Appendix F	Location Plan of Air Quality Monitoring Station			
Appendix G	Appendix G Dust Monitoring Data			
Appendix H	Appendix H Waste Flow Table			
Appendix I	Transportation Routes To/From the Site			
Appendix J	Statistics on Complaint, Notifications of Summons and Successf Prosecutions	iul		



EXECUTIVE SUMMARY

INTRODUCTION

- A1. The Project, Expansion of Wo Hop Shek Crematorium, is a Designated Project under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO) and is currently governed by a Environmental Permit (EP No. EP 329/2009) for the construction and operation of the Project.
- A2. In accordance with the Environmental Monitoring and Audit (EM&A) Manual for the Project, EM&A works for air quality monitoring and waste management should be carried out by Environmental Team (ET), Acuity Sustainability Consulting Limited (ASCL), during the construction phase of the Project.
- A3. This is the 6th Quarterly EM&A Report, prepared by ASCL, for the Project summarizing the monitoring results and audit findings of the EM&A programme at and around Wo Hop Shek Crematorium during the reporting period from 1 July 2021 to 30 September 2021.
- A4. The EM&A programme for this contract has covered environmental monitoring on construction dust level at selected NSRs and Contractor's environmental performance auditing in the aspects of construction dust, construction noise, water quality, waste management, Landscape and Visual and Ecology.

SUMMARY OF MAIN WORKS UNDERTAKEN & KEY MITIGATION MEASURES IMPLEMENTED

- A5. Key activities carried out in this reporting period for the Project included the following:
 - Fitting out
- A6. The major environmental impacts brought by the above construction works include:
 - Construction noise generation from fitting out
 - Waste generation from construction activities
- A7. The key environmental mitigation measures implemented for the Project in this reporting period associated with the above construction works include:
 - Reduction of noise from equipment and machinery on-site
 - Treatment of wastewater from fitting out through sedimentation tank
 - Sorting and storage of general refuse and construction waste



SUMMARY OF EXCEEDANCE & INVESTIGATION & FOLLOW-UP

- A8. No project-related exceedance in air quality monitoring, including 24-hour TSP and 1-hour TSP of the Action Level was recorded during the reporting period.
- A9. Weekly site inspections of the construction work by ET were carried out to audit the mitigation measures implementation status. Observations were recorded in the site inspection checklists and provided to the contractors together with the appropriate follow-up actions where necessary.

COMPLAINT HANDLING AND PROSECUTION

- A10.No project-related environmental complaint was received during the reporting period.
- A11. Neither notifications of summons nor prosecution was received for the Project.

REPORTING CHANGE

A12. There was no change to be reported that may affect the on-going EM&A programme.

SUMMARY OF UPCOMING KEY ISSUES AND KEY MITIGATION MEASURES

- A13.Key activities anticipated in the next reporting period for the Project will include the following:
 - Fitting out

A14. The major environmental impacts brought by the above construction works will include:

- Construction noise generation from fitting out
- Waste generation from construction activities
- A15. The key environmental mitigation measures for the Project in the coming reporting period associated with the above construction works will include:
 - Reduction of noise from equipment and machinery on-site
 - Treatment of wastewater from fitting out through sedimentation tank
 - Sorting and storage of general refuse and construction waste



1. Basic Project Information

1.1. BACKGROUND

The Food and Environmental Hygiene Department (FEHD) is responsible for the operation of public crematorium in Hong Kong including the Cremators at Wo Hop Shek Crematorium pursuant to Environmental Permit No. EP-329/2009. The existing Wo Hop Shek Crematorium (WHSC) was re-provisioned in February 2013. It comprises six body cremators, one bone cremator and three service halls. At the design stage, areas had already been reserved for the addition of two body cremators and one service hall. In order to cope with increasing demand for cremation sessions, Expansion of Wo Hop Shek Crematorium (the Project) is being taken forward in this juncture. This Project shall provide two new cremators at WHSC and one service hall for commissioning. Architectural Services Department (ArchSD) acts as the works agent for FEHD, is responsible for the project management of the project.

The Project consists of three construction phases. Phase I of the project was substantially completed in October 2012 while Phase II of the project was substantially completed in November 2013. The Project has been re-initiated as Phase III and Shing Hing Construction Co. Ltd. (the Contractor) has been awarded the construction contract for the Project with contract no. AL G513.

The scope of the Project comprises provision of:

- Two new body cremators;
- One new multi-purpose service hall;
- A full range of ancillary facilities; and
- Addition, alteration and modification works that are necessary for the additional cremators and service hall.


1.2. THE REPORTING SCOPE

This is the 6th Quarterly EM&A Report for the Project which summarizes the key findings of the EM&A programme during the reporting period from 1 July to 30 September 2021.

1.3. PROJECT ORGANIZATION

The Project Organization structure for Construction Phase is presented in Figure 1.1.



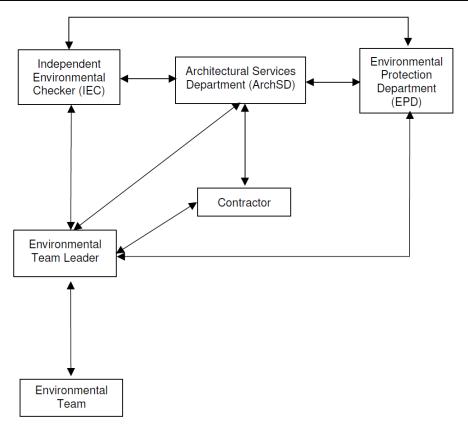

← ► Line of Communication

Figure 1.1 Project Organization Chart Contact details of the key personnel are presented in Table 1.1 below:

Table 1.1 Contact Details of Key Personnel

Party	Position	Name	Telephone no.
Shing Hing Construction Co Ltd	Site Agent	M.Y. Wong	2807-4665
Acuity Sustainability Consulting Limited	Environmental Team Leader	Kevin Li	2698-6833
Ove Arup & Partners Hong Kong Ltd	Independent Environmental Checker (IEC)	Sam Tsoi	2528-3031



1.4. SUMMARY OF CONSTRUCTION WORKS

Details of the major construction activities undertaken in this reporting period are shown in Table 1.2 below. The construction programme is presented in **Appendix A**.

Table 1.2 Summary of the Construction Activities Undertaken during the Reporting Period

	Terrou
Reporting Period	Construction Activities
July 2021	1. Fitting out
August 2021	1. Fitting out
September 2021	1. Fitting out



Reporting Period	Construction Activities



1.5. SUMMARY OF ENVIRONMENTAL STATUS

Environmental permit (EP) conditions under the EIAO, submission status under the EP and implementation status of mitigation measures had been reviewed and implemented on schedule. The status of required submissions under the EP (EP-329/2009) as of the reporting period for the Project are summarised in Table 1.3.

Table 1.3 Summary of Status of Required Submission for EP-329/2009 for the Project

EP/FEP Condition (EP-457/2013/C)	Submission	Submission date
Condition 1.12	Notification of Commencement Date of Construction of the Project	14 Mar 2020
Condition 2.3	Inception Report	13 Mar 2019
Condition 2.4	Tree Transplant Proposal	12 Apr 2019
Condition 2.5	Landscape Plan with Tree Preservation Proposal	14 Feb 2018
Condition 5.2a	Baseline Monitoring Report	21 Jan 2020
Condition 5.2b	Alternative Air Quality Monitoring Station	05 Oct 2019
Condition 5.4	Quarterly EM&A Report (July 2021 - September 2021)	13 Oct 2021

A summary of the valid permits, licences, and /or notifications on environmental protection for this Project is presented in Table 1.4.

Table 1.4 Summary of the Status of Valid Environmental Licence, Notification, Permit and Documentations

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Environmental Permit	EP-329/2009	Throughout the Contract	-
Notification of Construction Works under the Air Pollution Control (Construction Dust) Regulation (Form NA)	Ref. Number: 455614	Throughout the Contract	-



Wastewater Discharge Licence	WT00034798-2019	10 Oct 2020 – 31 Oct 2024	-
Chemical Waste Producer Registration	5213-632-S4245-01	Throughout the Contract	-
Construction Noise Permit (24 hours) (Renewal)	GW-RN0888-20	13 Jan 2021 – 12 July 2021	-
Construction Noise Permit (24 hours) (Renewal)	GW-RN0401-21	13 Jul 2021 – 12 Jan 2022	-
Billing Account for Disposal of Construction Waste	7032841	Throughout the Contract	-

The status for all environmental aspects is presented in Table 1.5.

Table 1.5 Summary of Status for Key Environmental Aspects under the Updated EM&A Manual

Parameters	Status		
Dust			
Baseline Monitoring	The baseline dust monitoring result has been reported in Baseline Monitoring Report and submitted to EPD under EP Condition 5.2a.		
Impact Monitoring	On-going		
Waste Management			
Mitigation Measures in Waste Monitoring Plan	On-going		
Environmental Audit			
Site Inspection covering Measures of Air Quality, Noise Impact, Water Quality, Waste, Ecological Quality, Landscape and Visual	On-going		

Other than the EM&A work by ET, environmental briefings, trainings and regular environmental management meetings were conducted, in order to enhance environmental awareness and closely monitor the environmental performance of the contractors.



The EM&A programme has been implemented in accordance with the recommendations presented in the approved EIA Report and the Updated EM&A Manual. A summary of implementation status of the environmental mitigation measures for the construction phase of the Project during the reporting period is provided in **Appendix C**.



2. Monitoring Results

2.1. MONITORING PARAMETERS

The impact monitoring had been carried out in accordance with section 2.6 of the approved EM&A Manual to determine the 1-hour and 24-hour total suspended particulates (TSP) levels at the monitoring locations in the reporting period.

The sampling frequency of at least once in every 6 days, shall be strictly observed at the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least 3 times in every 6 days should be undertaken when the highest dust impact occurs.

General meteorological conditions (wind speed, direction and precipitation) and notes regarding any significant adjacent dust producing sources had also been recorded throughout the impact monitoring period.

2.2. Monitoring Locations

Due to the disagreement of occupants in establishment of air quality monitoring station at their private permits, both of the original proposed dust monitoring locations were rejected. Two alternative air monitoring stations Fung Kai Liu Yun Sum Memorial School and Fanling Government School had been proposed by ET and approved by IEC. Two designated air monitoring locations were identified and agreed with IEC and EPD. Details of air monitoring stations are described in Table 2.2. The location plan of air quality monitoring stations is shown in **Appendix F**.

Table 2.2 Location of the Dust Monitoring Stations

Air Quality Monitoring Station	Dust Monitoring Station
A10	Fung Kai Liu Yun Sum Memorial School
A20	Fanling Government School

2.3. MONITORING DATE, TIME, FREQUENCY AND DURATION

A summary of impact monitoring duration, sampling parameter and frequency is presented in Table 2.3.



 Table 2.3
 Summary of Impact Monitoring Programme

Impact Monitoring	Duration	Sampling Parameter	Frequency
Dust	1-hour continuous measurement	1-hour TSP	3 times per six days
Dust	24-hour continuous sampling	24-hour TSP	Once per six days

2.4. RESULT SUMMARY

According to our field observations, the major dust source identified at the designated air quality monitoring station in the reporting period are summarised in Table 2.4.

Table 2.4 Observation at Dust Monitoring Station

Monitoring Station	Major Dust Source
A10	Nearby traffic
A20	Nearby traffic

Air quality impact monitoring for the reporting period was carried out on the dates below:

Reporting Month	Measurement Date
July 2021	05, 10, 16, 22 and 28 July 2021
August 2021	03, 09, 14, 20 and 26 August 2021
September 2021	01, 07, 13, 18, 24 and 29 September 2021

The results for 1-hour TSP and 24-hour TSP are summarized in Table 2.5 and Table 2.6. The measurement data and details of influencing factors such as weather conditions and site observation are presented in **Appendix G**.

Table 2.5 Summary of 1-hour TSP Monitoring Results

Monitoring Location	Range (μg/m³)	Action Level (μg/m³)	Limit Level (µg/m³)
A10	40 - 61	290	500
A20	41 - 66	291	500



Table 2.6 Summary of 24-hour TSP Monitoring Results

Monitoring Location	Range (μg/m³) Action Level (μg/m³)		Limit Level (μg/m³)	
A10	15 - 62	169	260	
A20	10 - 52	167	260	



3. Waste

3.1. WASTE RECORD OF REPORTING PERIOD

The waste generated from this Project includes inert construction and demolition (C&D) materials, and non-inert C&D materials. Non-inert C&D materials are made up of general refuse, vegetative wastes and recyclable wastes such as plastics and paper/cardboard packaging waste. Steel materials generated from the project are also grouped into non-inert C&D materials as the materials were not disposed of with other inert C&D materials. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting period are summarised in Table 3.1. Details of cumulative waste management data are presented as a waste flow table in **Appendix H.**

Table 3.1 Quantities of Waste Generated from the Project from July to September 2021

Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of C&D Wastes Generated Monthly						
Reporting Month	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper / cardboard packaging	Plastics (see Note)	Chemical Waste	Others, e.g. general refuse
	(in ,000kg)	(in,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)
July 2021	19.70	0	0	0	7.73	0	0	0	0	0	11.97
August 2021	20.29	0	0	0	14.95	0	0	0	0	0	5.34
September 2021	219.20	0	0	0	214.71	0	0	0	0	0	4.49

Notes:

(1) Plastics refer to plastic bottles / containers, plastic sheets / foam from packaging material



3.2. MITIGATION MEASURES TO WASTE PRODUCTION

Mitigation measures adopted for reducing waste production are summarized in Table 3.2.

Table 3.2 Mitigation measures adopted for waste reduction

	ruble 512 Finingation measures adopted for waste reduction					
Types of Waste	Mitigation Measures					
Non-inert C&D Wastes	1. On-site segregation was adopted to wastes to enhance the reuse and recycling of non-inert C&D wastes. Separated containers are provided for temporary storage of different types of non-inert wastes, including the deployment of three-colour recycle bins for paper, aluminium cans, and plastic bottle recycling. Three-colour recycle bins					
	Enclosed rubbish bin for general waste					



Types of Waste	Mitigation Measures		
	Skip for non-inert C&D waste		
	2. Careful design and planning with good site management to minimize over ordering and generation of waste materials.		
	3. Reuse non-inert C&D materials when possible to reduce the amount of C&D waste. The timber for formwork was reused on site.		
	Timber for formwork was reused on-site		
Inert C&D Wastes	1. Excavated inert C&D materials were separately stored for subsequent backfilling, approximately 614 tonnes of excavated inert materials were stored in construction material storage area with coverage of impervious sheeting for on-site backfilling.		



Types of Waste	Mitigation Measures
	No excavated material was stored at material storage area in the reporting period. 2. Surplus excavated materials were delivered to public fill reception facilities.
Chemical Wastes	1. Unused chemicals or chemicals with remaining functional capacity were reused as far as practicable. Chemical with remaining functional capacity was stored in a designated area and reused on-site.



4. Summary of Monitoring Exceedance, Complaints, Notification of Summons and Prosecutions

The Environmental Complaint Handling Procedure is shown in below Figure 4.1:

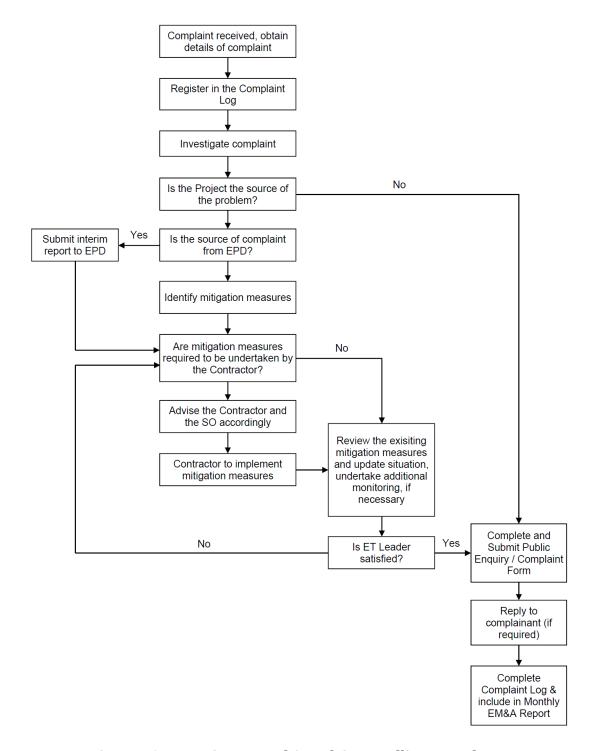


Figure 4.1 Environmental Complaint Handling Procedures



Air quality monitoring was conducted in the reporting period and no project-related exceedance of the Action Level was recorded during the reporting period.

No notification of summons and prosecution was received in the reporting period.

Statistics on complaints and regulatory compliance are summarized in **Appendix J**.



5. EM&A SITE INSPECTION

Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, site inspections were carried out at the site portions list in Table 5.1 below.

Table 5.1 Summaries of Site Inspection Record

Date	Inspected Site Portion	Time
09 July 2021	Wo Hop Shek Crematorium	10:15 - 10:30 AM
14 July 2021	Wo Hop Shek Crematorium	10:30 - 10:50 AM
21 July 2021	Wo Hop Shek Crematorium	10:00 - 10:15 AM
28 July 2021	Wo Hop Shek Crematorium	10:25 - 10:40 AM
04 August 2021	Wo Hop Shek Crematorium	10:00 - 10:20 AM
10 August 2021	Wo Hop Shek Crematorium	10:15 - 10:30 AM
18 August 2021	Wo Hop Shek Crematorium	10:00 - 10:20 AM
25 August 2021	Wo Hop Shek Crematorium	10:15 - 10:30 AM
01 September 2021	Wo Hop Shek Crematorium	10:15 - 10:30 AM
07 September 2021	Wo Hop Shek Crematorium	10:30 - 10:45 AM
15 September 2021	September 2021 Wo Hop Shek Crematorium	
23 September 2021	3 September 2021 Wo Hop Shek Crematorium	
29 September 2021	Wo Hop Shek Crematorium	10:15 – 10:40 AM

Environmental deficiencies were observed during weekly site inspection. Key observations during the site inspections and during the reporting period are summarized in **Table 5.2**.

According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents are implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix C**.

According to the Environmental Permit (EP) clause 3.6, route 2 and route 5 shall not be used as transportation routes during construction, which was attached in **Appendix I**. The measures implemented to comply with the EP's requirement are listed as follows:

- 1. Induction training including the proper transportation routes use
- 2. Posting extracts of the transportation route to/from the site outside the entrance
- 3. Toolbox training provided to the drivers entering the site

Measure no.2 of the above was observed during the site inspections.

In order to comply with the requirement of the EP clause 3.5, the implementation of all landscaping and visual mitigation measures in accordance with the landscape plan approved was audited in the reporting period.

Bi-weekly checking for the transplanted tree was conducted during the site inspections. No major observation was found related to the landscaping and visual.



Table 5.2 Site Observations

Date	Environmental Observations	Follow-up Status	
09 Jul 2021	Observation(s)	Nil.	
(Site inspection)	1. No major observation was observed.	IVII.	
	Observation(s)		
14 Jul 2021	1. No major observation was observed.	N/I	
(Site inspection)	Denvis des(e)	Nil.	
	Reminder(s) 1. The exposed soil should be sprayed with water.		
	Observation(s)		
	1. No major observation was observed.		
21 Jul 2021	1. Ito major observation was observed.	Nil.	
(Site inspection)	Reminder(s)		
	1. Housekeeping should be maintained.		
	Observation(s)		
28 Jul 2021	1. No major observation was observed.	_	
(Site inspection)		Nil.	
,	Reminder(s)		
04 Aug 2021	Stagnant water should be cleared after rain. Observation(s)		
(Site inspection)	1. No major observation was observed.	Nil.	
10 Aug 2021	Observation(s)		
(Site inspection)	1. No major observation was observed.	Nil.	
18 Aug 2021	Observation(s)	No.	
(Site inspection)	1. No major observation was observed.	Nil.	
	Observation(s)		
25 Aug 2021	1. No major observation was observed.		
(Site inspection)		Nil.	
(= 110 = 110 p = 110 m)	Reminder(s)		
01 Cam 2021	1. Stagnant water should be removed.		
01 Sep 2021 (Site inspection)	Observation(s)	Nil.	
(Site Hispetholi)			



Date	Environmental Observations	Follow-up Status
	1. No major observation was observed.	
	Reminder(s)	
	1. Stagnant water should be removed.	
	2. Housekeeping should be maintained.	
	Observation(s)	
	1. No major observation was observed.	
07 Sep 2021		Nil.
(Site inspection)	Reminder(s)	IVII.
	1. Housekeeping should be maintained.	
	2. Cement bags should be covered after use.	
	Observation(s)	
	1. Chemicals in-use should be placed on drip tray.	
15 Sep 2021		 Chemicals in-use was placed on drip tray.
(Site inspection)	Reminder(s)	1. Girchileais in use was placed on arrp tray.
	1. Stagnant water should be removed.	
	2. Housekeeping should be maintained.	
	Observation(s)	
00.0	1. No major observation was observed.	
23 Sep 2021	D (1)	Nil.
(Site inspection)	Reminder(s)	
	 Stagnant water should be removed after rain. Housekeeping should be maintained. 	
	Observation(s)	
	1. No major observation was observed.	
	1. No major observation was observed.	
29 Sep 2021	Reminder(s)	Nil.
(Site inspection)	1. Dusty materials should be covered with impervious	IVII.
	sheeting entirely.	
	2. Housekeeping should be maintained.	



6. CONCLUSIONS AND RECOMMENDATIONS

This is the 6^{th} Quarterly EM&A Report for the Project which summarizes the key findings of the EM&A programme during the reporting period from 1 July to 30 September 2021, in accordance with the EM&A Manual and the requirement under EP – 329/2009.

Air quality monitoring was conducted in the reporting period and no project-related exceedance of the Action Level was recorded during the reporting period.

Weekly environmental site inspection was conducted during the reporting period. Some observations were observed during site inspection and rectifications had been accomplished by contractor within a week after site inspection. The environmental performance of the project was therefore considered satisfactory. Contractor was reminded to maintain the tidiness of the project site.

No environmental complaint was received in the reporting period.


No notification of summons or prosecution was received since commencement of the Contract.

The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.




APPENDIX A: MASTER PROGRAMME




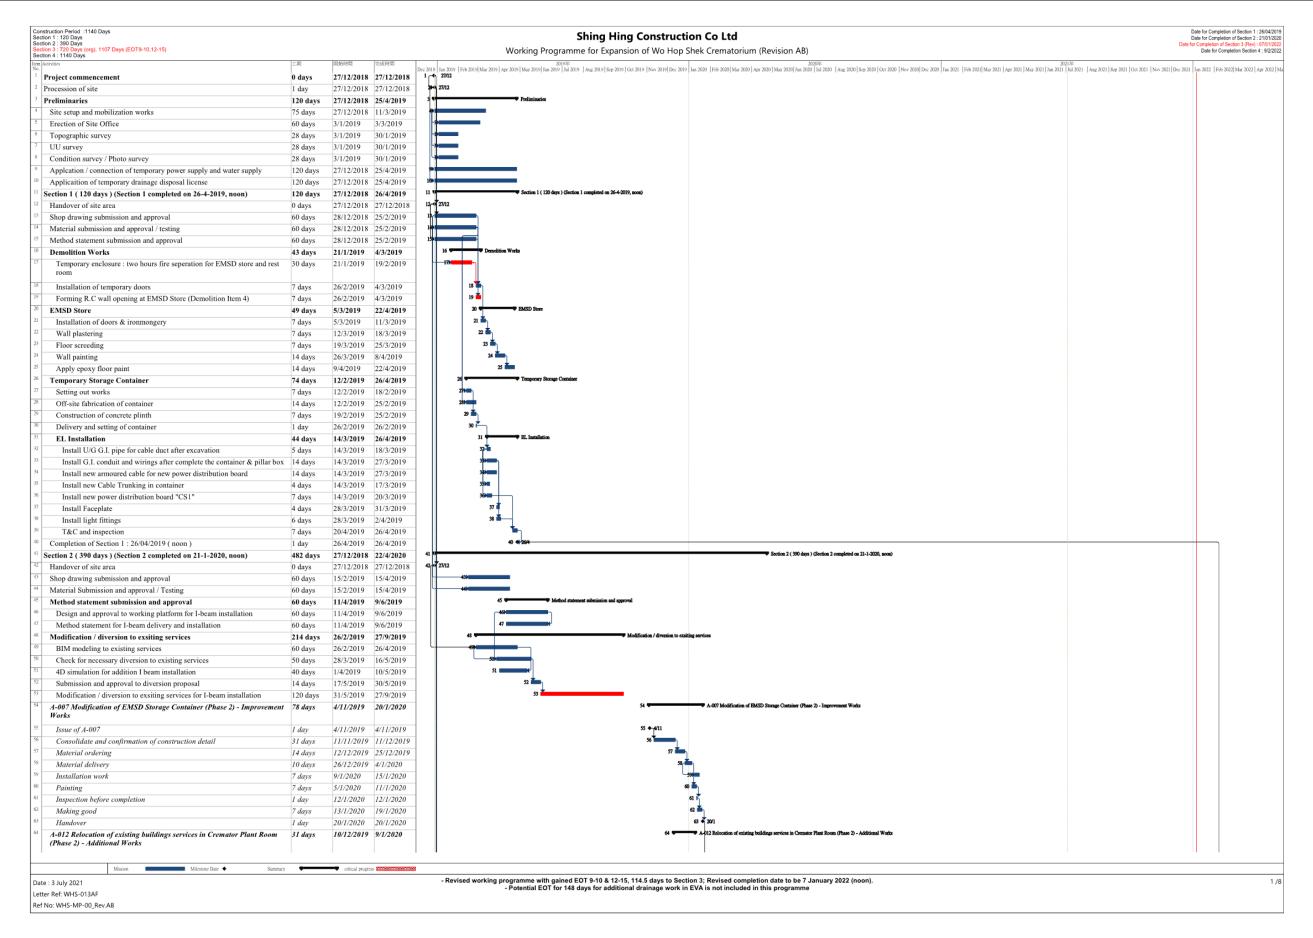




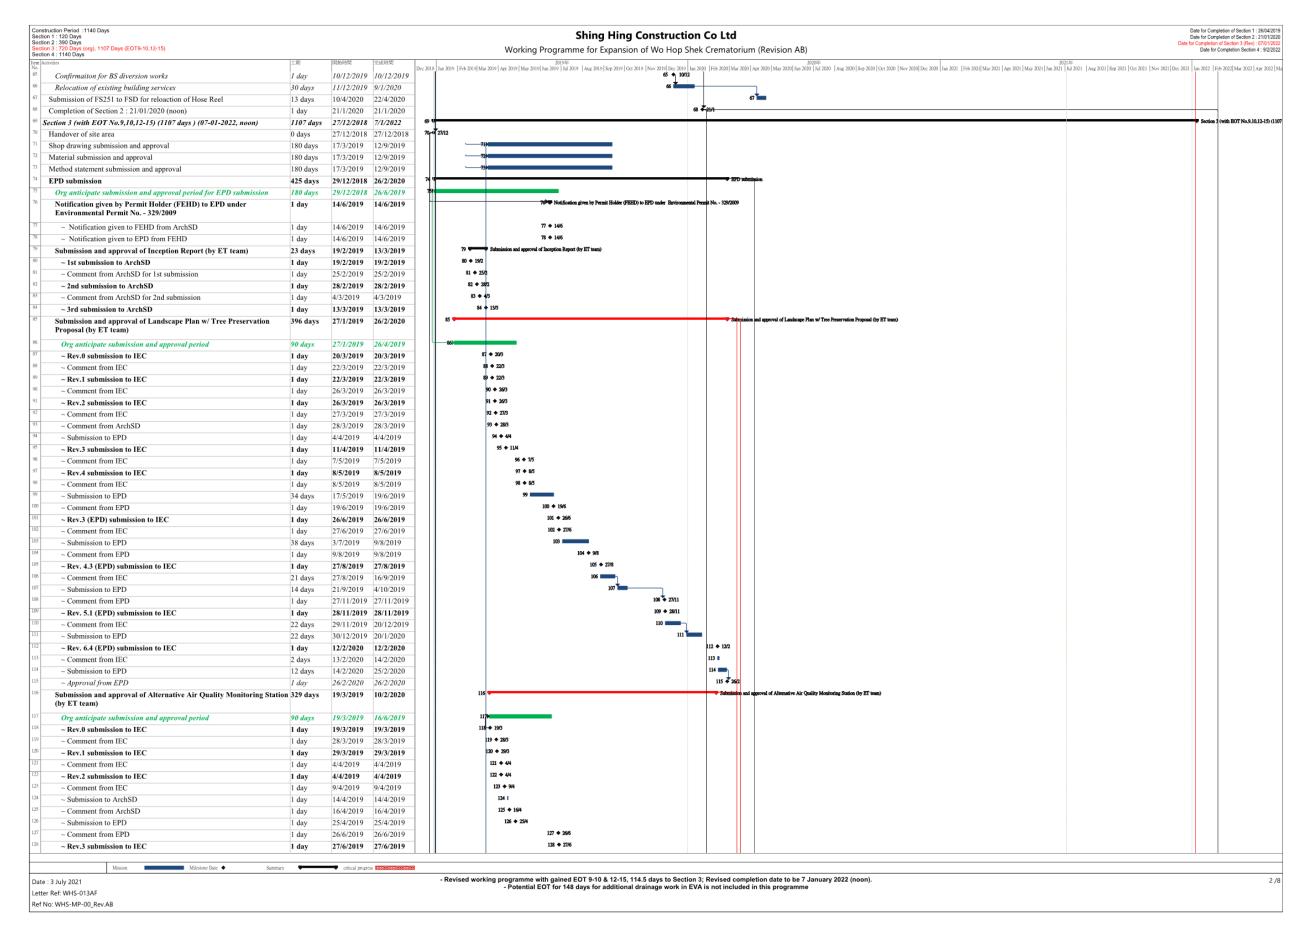




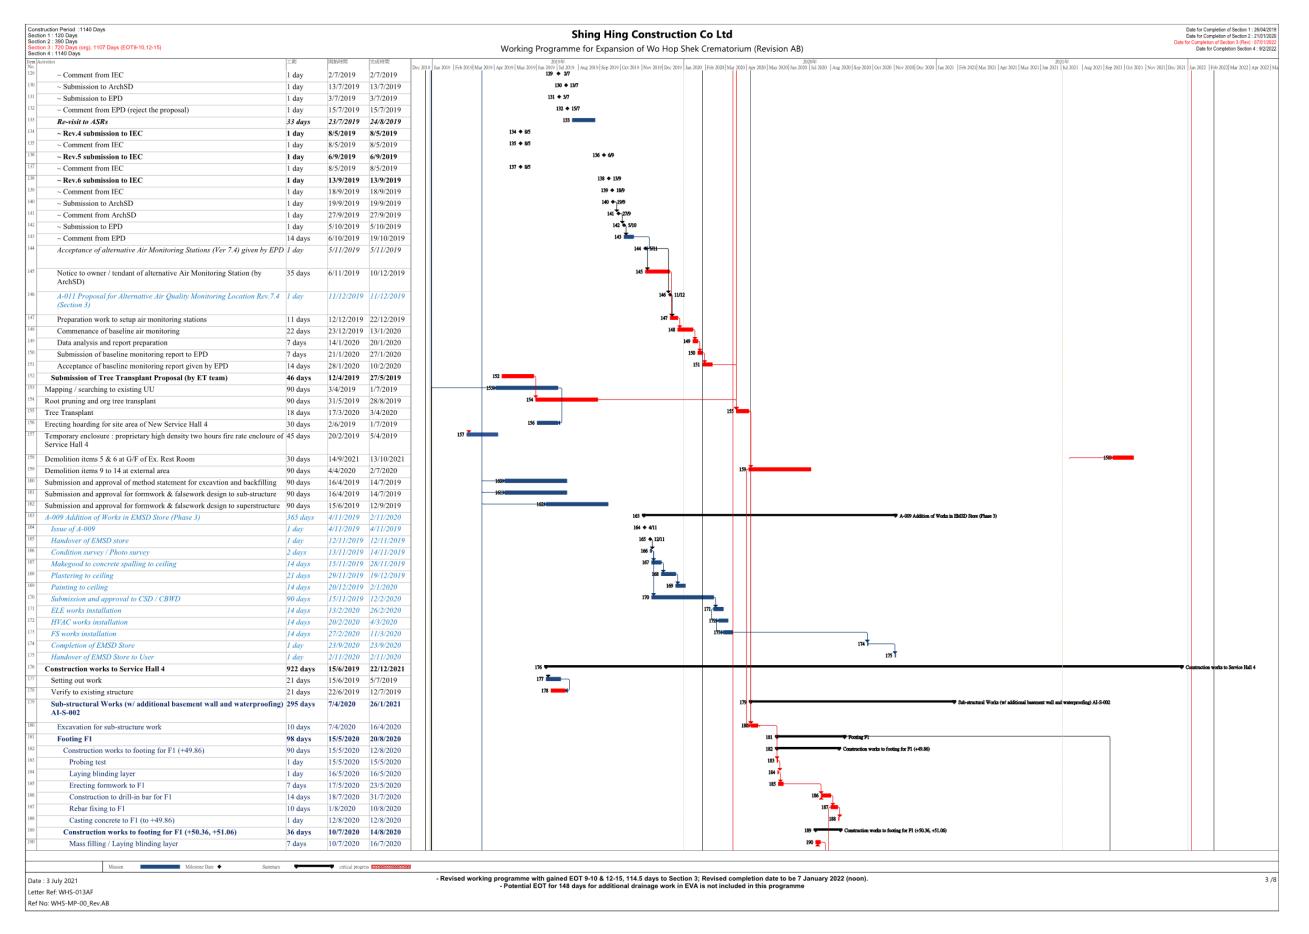




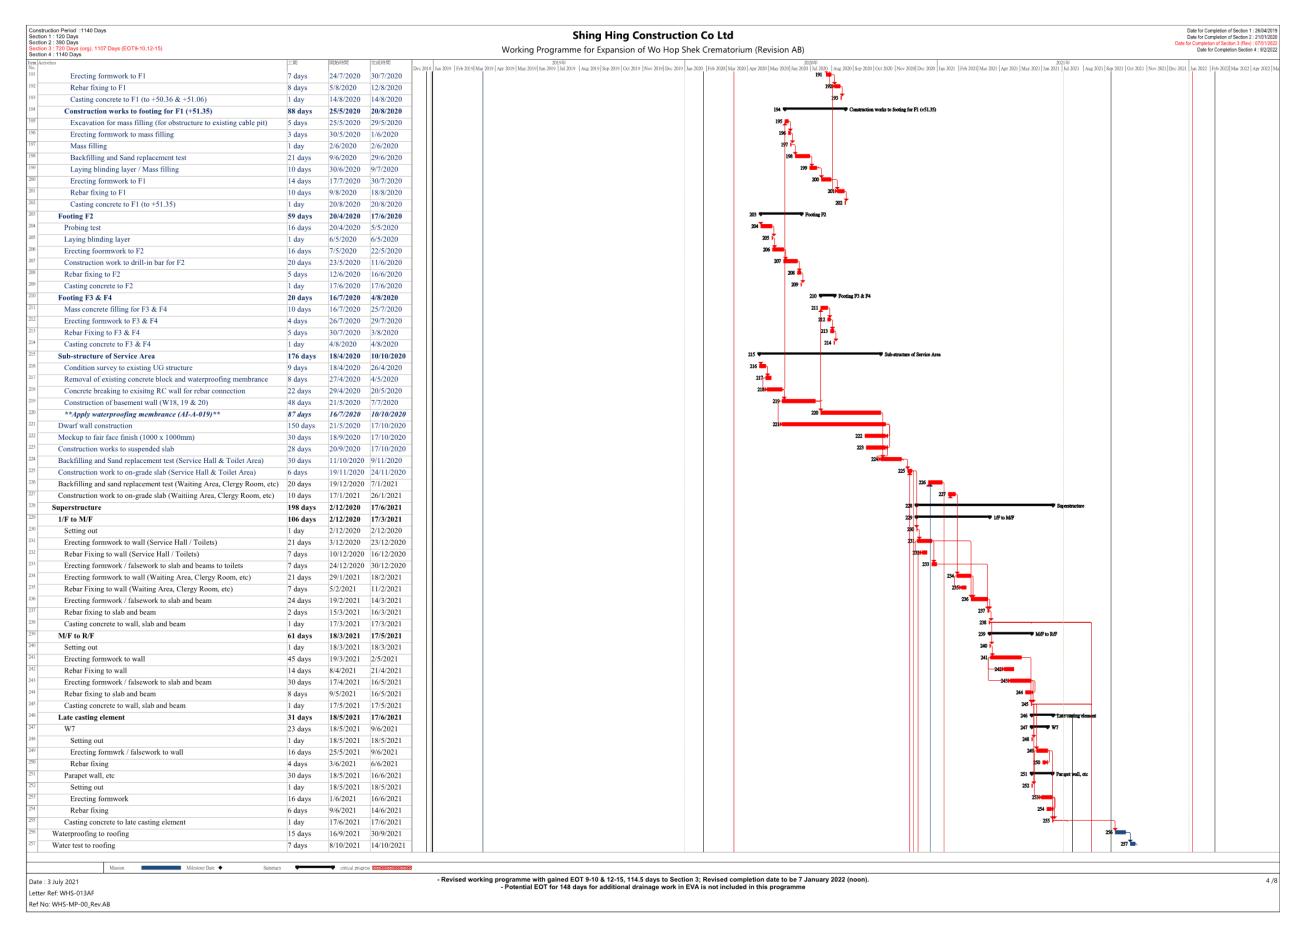




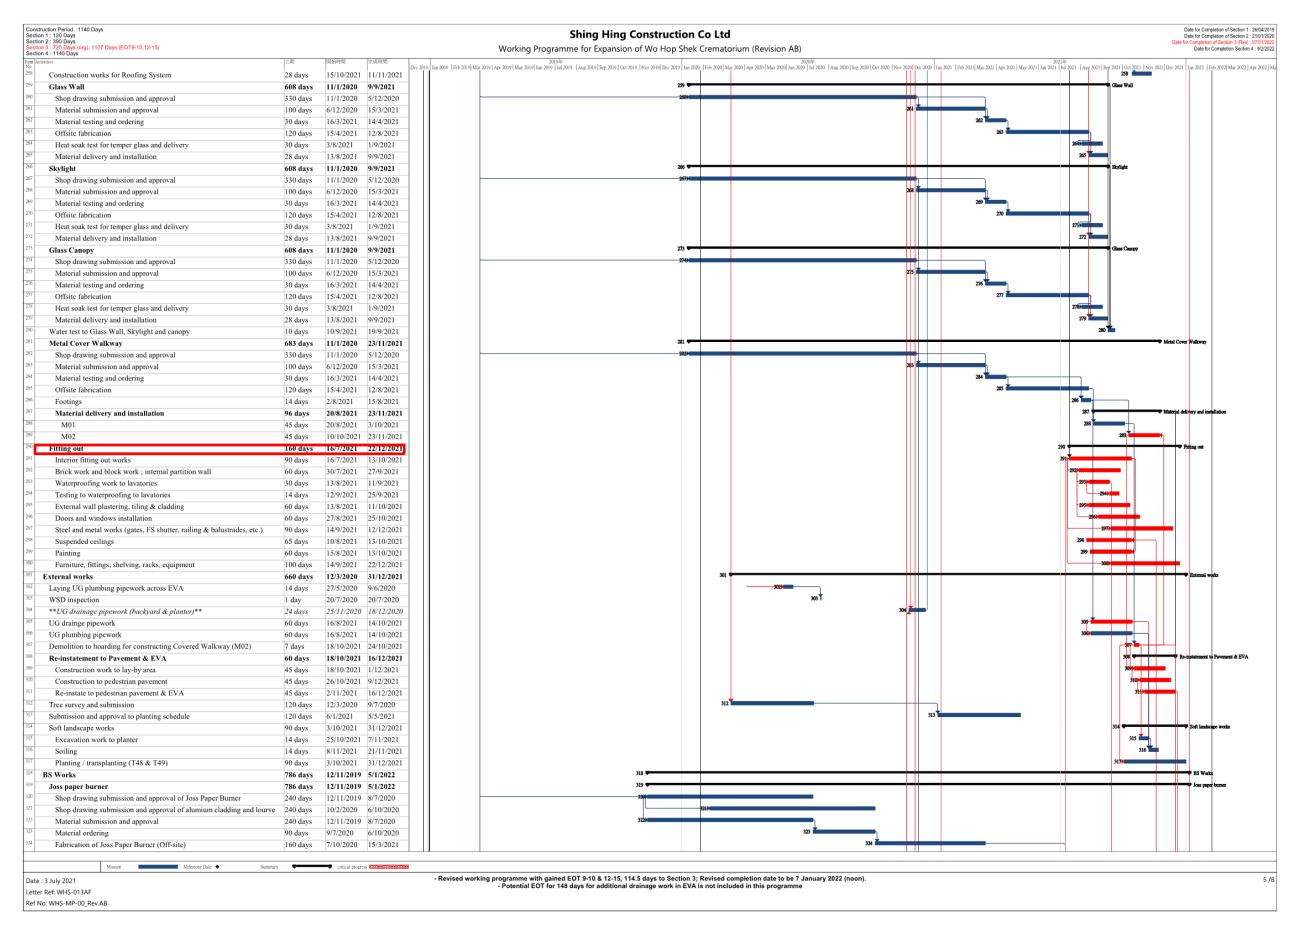




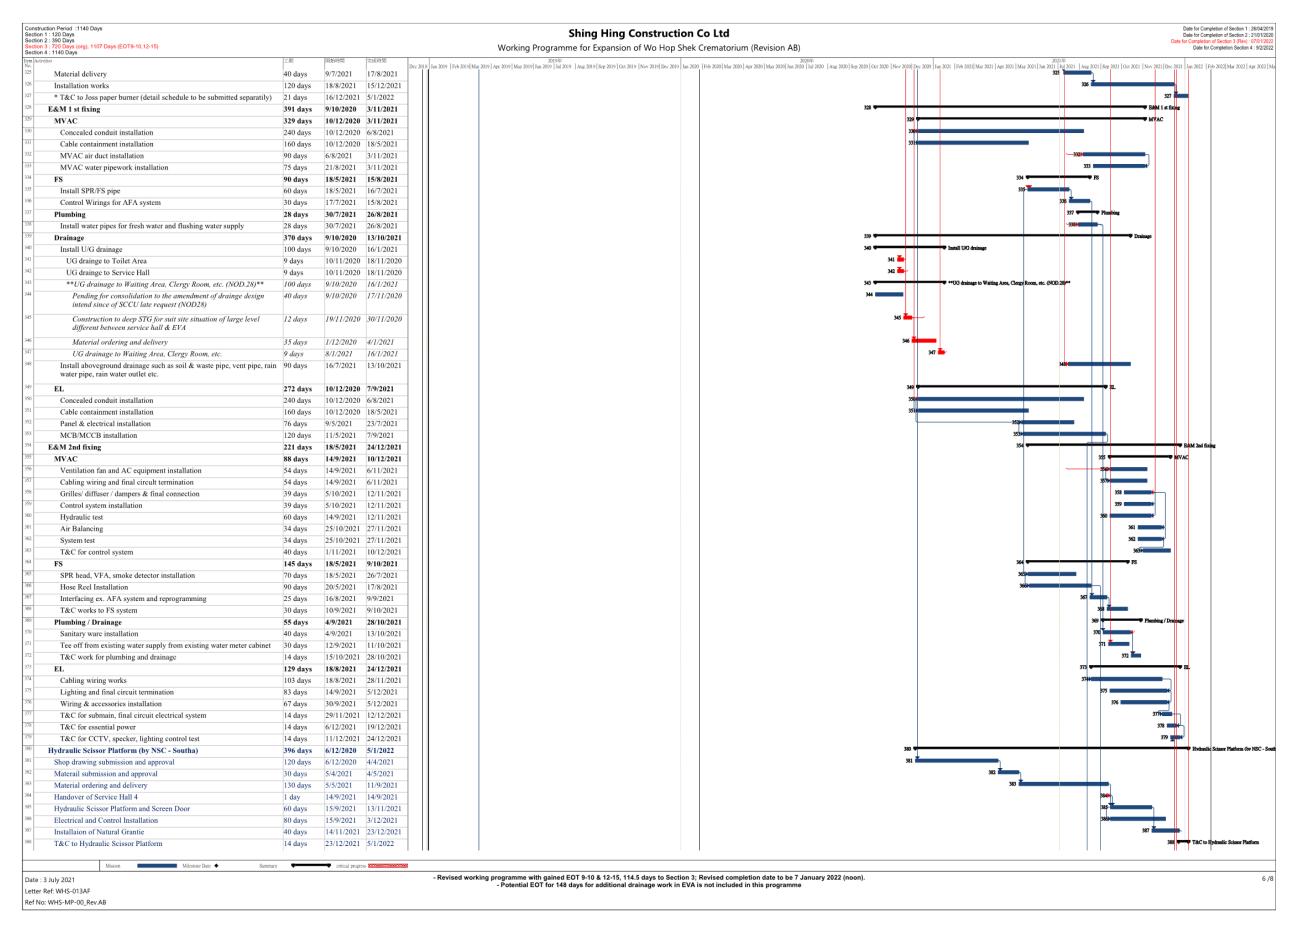



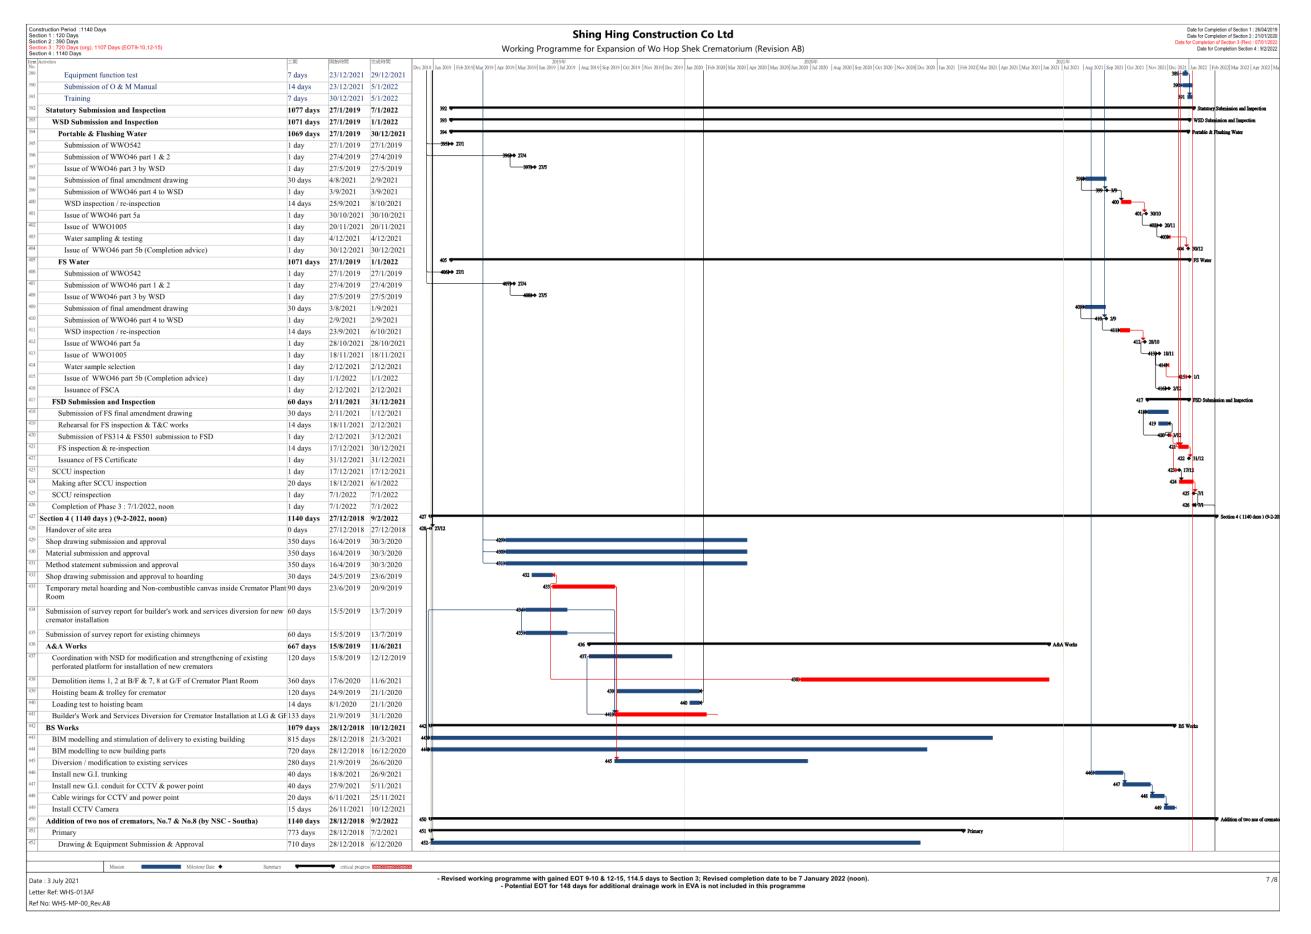




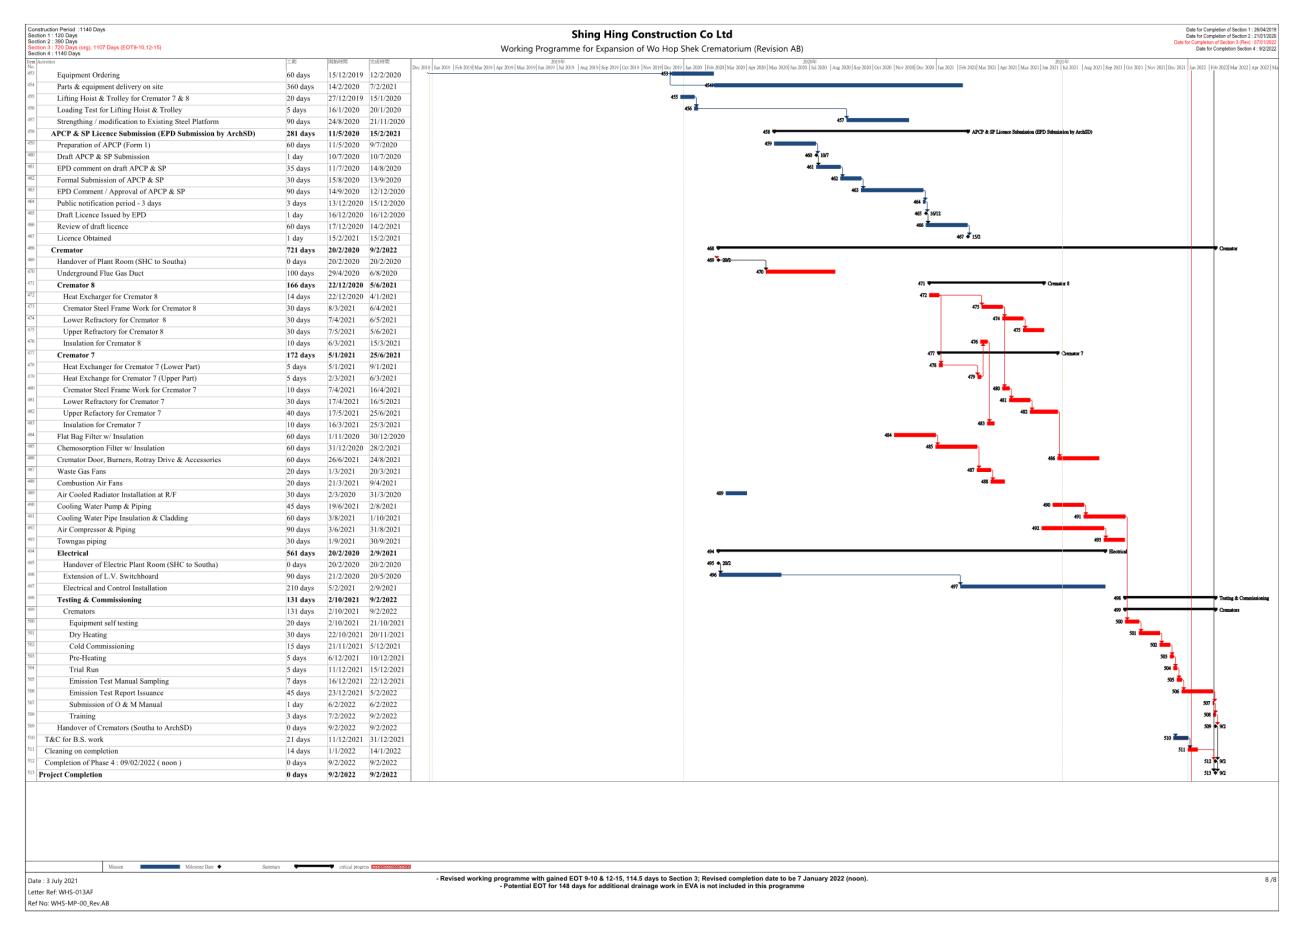



APPENDIX B: WORK AREA FOR THE CONTRACT NO. AL G513



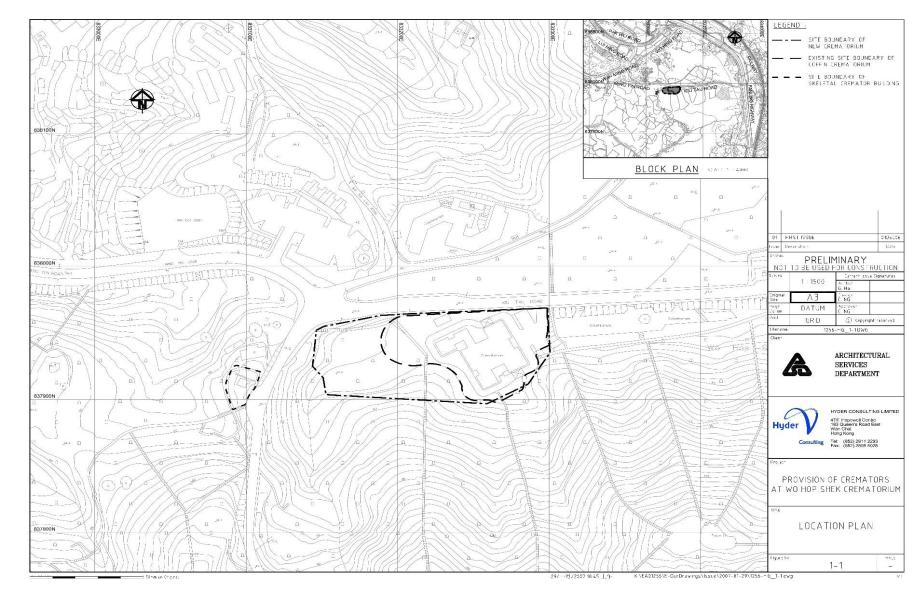



APPENDIX C: SUMMARY OF IMPLEMENTATION STATUS OF Environmental Mitigation



	C	and the part note					
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
Air (Cons	truction	Phase)					
S.3.3.5			New Cremators in the New Crematorium / prior to operation	FEHD	Construction Phase	APCO	NA
S.3.9		Asbestos Investigation:	Incense burner,	Arch SD,	Construction Phase	APCO	NA
S.3.9.2			coffin and Registered skeletal Asbestos Crematorium / Consultant, Prior to any demolition Registered Asbestos		AIR and AAP		
S.3.9.3		■ If any ACM are identified in the existing crematorium, an asbestos abatement plan shall be submitted to EPD prior to any asbestos abatement works.	work commencing	Contractor			
S.3.9.4		The following precautionary and mitigation measures shall be implemented during the removal of ACM:					
		■ Enclosure of the work area.					
		■ Containment and sealing for the asbestos containing waste.					
		■ Provision of personal decontamination facility.					
		■ Use of personal respiratory/protection equipment.					
		Use of vacuum cleaner equipped with high-efficiency air particulate (HEPA) filter for cleaning up the work area.					
		■ Carrying out air quality monitoring during the asbestos abatement works.					



	Quart	erry EM&A Report No.0				500 500 600	
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.3.9.5		The following qualified personnel shall be appointed to carry out the asbestos abatement works:					NA
		■ Registered asbestos contractor for carrying out the asbestos removal works.					
		Registered asbestos supervisor for supervising the asbestos abatement works.					
		Registered asbestos laboratory for monitoring the air quality during the asbestos abatement works.					
		Registered asbestos consultant for supervising and certifying theasbestos abatement works.					
S.3.9.7 -		Other Site Management:					NA
S.3.9.9							
S.3.9.7		The asbestos materials in each building/premises must be abated before other contractors/trades are allowed to work in the building/premises.					NA
S.3.9.8		Tight security measures shall be taken at the asbestos abatement works site to prevent any disturbance to ACM that may result from the stealing of valuable items on site such as electrical cable and copper pipes. It is recommended that priority shall be given for the abatement of all friable ACM.					NA
S.3.9.9		As different contractors may be working on-site at the same time, the following measures should be considered:					NA
		■ If there is a sensitive receptor around the area, conduct environmentalair monitoring at this off-site receptor.					
		Submit to EPD a completion report, including photos and air monitoring results, immediately after completion of asbestos abatement work for every work zone.					
S.3.9.9		As different contractors may be working on-site at the same time, the following measures should be considered:					NA
		■ If there is a sensitive receptor around the area, conduct environmentalair monitoring at this off-site receptor.					
		■ Submit to EPD a completion report, including photos and air monitoring results, immediately after completion of asbestos abatement work for every work zone.					



	Quarterly Electricia								
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status		
S.3.10.1 - S.3.10.2		The contractor has a responsibility to notify EPD for undertaking any 'notifiable' works prior to the commencement of such works. In addition, the contractor is also required to fulfil specific dust control requirements given in the APCO Regulation's Schedule for specific jobs.	Prior to 'notifiable' works including Construction of the foundation of a building and construction of the superstructure of a building	Contractor	Construction Phase	Air Pollution Control (Construction Dust) Regulation APCO	Implemented		
S.3.10.3 - S.3.10.4	S.2.9.1 - S.2.9.3	Good site management / practices to avoid / minimise incidences of dust emissions: Site Boundary and Entrance	Project Site / Construction and Demolition	Contractor	Construction Phase	Air Pollution Control (Construction Dust) Regulation	Implemented		
		 Vehicle washing facilities including a high pressure water jet shall be provided at every discernible or designated vehicle exit point. The area at which vehicle washing takes place and the section of the road between the washing facilities and the exit point shall be paved with concrete, bituminous or hardcore material. 				APCO			
		Access Haul Roads and Unpaved Areas Each and every main haul road shall be paved with concrete, bituminous hardcore materials or metal plates, and kept clear of dusty materials. Or							
		■ Unpaved haul roads and areas shall be sprayed with water so as to keep the entire road surface wet.							



<u> </u>	uai tt	THY EMICA REPORT NO.0				CONSULTING	LIMITED
	M&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
		Excavated Materials					
		■ Any stockpile of dusty material shall be either: (a) covered entirely by impervious sheeting. (b) placed in an area sheltered on the top and the three sides. or (c) sprayed with water or a dust suppression chemical so as to maintain the entire surface wet.					
		Exposed Earth					
		■ Exposed earth shall be properly treated by compaction, hydroseeding, vegetation planting or seating with latex, vinyl, bitumen within six monthsafter the last construction activity on the site or part of the site where the exposed earth lies.					
		Loading, Unloading or Transfer of Dusty Materials					
		All dusty materials shall be sprayed with water immediately prior to any loading or transfer operation so as to keep the dusty material wet.					
		Debris Handling					
		Any debris shall be covered entirely by impervious sheeting or stored ina debris collection area sheltered on the top and the three sides.					
		■ Before debris is dumped into a chute, water shall be sprayed so that itremains wet when it is dumped.					
		Transport of Dusty Materials					
		■ Vehicles used for transporting dusty materials/spoils shall be covered with tarpaulin or similar material. The cover shall extend over the edges of the sides and tailboards.					
		Site Clearance					
		■ The working area for the uprooting of trees, shrubs, or vegetation or the removal of boulders, pole, pillars shall be sprayed with water immediately before, during and immediately after the operation so as to maintain theentire surface wet.					
		■ All demolished items shall be covered by impervious sheeting or placed in a spot with shelters on top and three sides within a day of the demolition.					
		■ Workers at all levels should be co-operative to avoid dust generation and dispersion to the surrounding environment.					



EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
Air (EM&	A for Co	nstruction Phase					
S.11.2.4 - S.11.2.5	S.2.5 S.2.6	Conduct baseline and regular 1-hr and 24-hr TSP monitoring at 2 measurement locations at a 6-day frequency	A22a and A22b / Baseline monitoring prior to construction works / Regular monitoring throughout construction period	Contractor	Construction Phase	EIAO	Implemented
		ion Phase)					
S.4.4.9 - S.4.4.10	S.3.2.1 - S.3.2.2	Good Site Practice and Noise Management: Only well-maintained plant shall be operated on site and the plant shall be regularly serviced during the construction works.	Work site / Construction phase	Contractor	Construction Phase	GW-TM & NCO	Implemented
		■ Plant used intermittently shall be turned off or throttled down when notin active use.					
		■ Plant that is known to emit noise strongly in one direction shall be oriented to face away from NSRs.					
		Silencers, mufflers and enclosures for plant shall be used where possible and maintained adequately throughout the works.					
		■ Mobile plant shall be sited away from NSRs.					
		■ Stockpiles of excavated materials and other structures such as site buildings shall be used effectively to screen noise from the works.					
		■ PME shall be well maintained and use properly on site to minimise the any excessive noise generated.					
Land Con	taminat	ion (Construction Phase)					1
		Remedial Action Plan:	All areas	Contractor	Construction Phase	Waste Disposal	



EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.5.7.2		If large amounts of contaminated soil (say 500m³) are found following further site investigation after the decommissioning of the crematorium, remediation options such as bioremediation for organics should be considered. Although disposal of smallamount of contaminated soil to landfills might be considered as an economic and acceptable option for remediation, it should be considered as the last resort if all remediation options including reuse are considered to be inappropriate or infeasible.	requiring remedial works in Project site			Ordinance (Cap.354) Waste Disposal (Chemical Waste) Regulations Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes CAP	NA
S.5.7.3		■ If disposal to landfills is chosen as the remediation measure, the criteria set primarily of Toxicity Characteristic Leaching Procedure (TCLP) limits, as stated in Annex E in the GN) should be met.				ProPECC Note PN3/94 Dutch A, B, C	NA
		At least three soil samples should be taken from the most contaminated area(s) and tested for TCLP for a full suite of parameters (16 metals) asstated in Table E1 in Annex E in the GN.				Classificati-on system	
		■ If the testing result shows that any of the TCLP limits cannot be met, the soil shall be treated by cement stabilization and further tested for TCLP prior to landfill disposal or treated as chemical waste and disposed of at the Chemical Waste Treatment Centre (CWTC).				WPCO Technical Memorandum on Standards for Effluents	
S.5.7.4		All soil treated as a chemical waste, shall be collected by a registered chemical waste contractor and the Waste Disposal (Chemical Waste) Regulations under the Waste Disposal Ordinance (Cap.354) shall be observed. Reference shall be made to the Registration of Chemical Waste Producers and Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes, issued by EPD.				Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters (TM)	NA



EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.5.7.6		Confirmatory Soil Sampling					NA
		 In order to confirm the extent of the soil contamination and if the contaminated soil should be removed or treated, confirmatory soil sampling shall be carried out during the remediation works. This shall consist of five to six samples in each location where soil contamination is identified from SI works. The locations will be to the north, south, east and west of the location where contaminated soil is found. Two locations should also be above and below the location (in terms of elevation) where contaminated soil is found. 					
		If analytical results exceed the Dutch B Levels or other agreed remedialtarget suggested in a supplementary CAR, the contaminated area shall be extended and further confirmatory sampling shall be carried out until no further contamination is encountered.					
S.5.8	S.4	Further Site Investigation	Areas that are currently in use	Contractor	Construction Phase	Interim CAR and RAP	NA
S.5.8.1	S.4.1 - S.4.7	Further site investigations in areas that are currently in use and cannot be accessed are required. These areas include the transformer room, dangerous goods stores, day tank room, fuel pump room, sunken fuel pipe and cremator.	and cannot be accessed, including the transformer room, dangerous			ProPECC Note PN3/94 Guidance Notes for Investigation and Remediation of	
S.5.8.2		The demolition contractor shall carry out further site investigations, after the decommissioning of the existing crematorium and skeletal cremator building.	goods stores, day tank room, fuel pump			Contaminated Sites of Petrol Filling Stations, Boatyards	
S.5.8.3		Potential contaminants in the soils have been identified in CAP and the parameters to be analysed for soils at different locations are summarised in Table 5-3 in S.5.8.3.	room, sunken fuel pipe and cremator.			and Car	



	Quarterly Liviati Report 10.0									
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status			
S.5.8.4		Sampling and analysis plans for these investigations shall be prepared and submitted to EPD for approval prior to any of these investigation works. Supplementary CAR and RAP shall be prepared to describe the results and findings of these site investigations and, if necessary, any remedial works.	After the decommissioni ng of the existing crematorium and skeletal cremator building.			Repair / DismantlingWorkshop s				
Land Con	taminat	ion (EM&A)								
S.11.2.9	S.4.1	Further Site Investigation: Conduct further site investigation for Petroleum hydrocarbons	After decommissioni	Contractor	Construction Phase	Interim CAR & RAP	NA			
S.11.2.15	S.4.7	and PAH in soil samples.	ng, prior to							
3.11.2.13	3.4.7	Conduct further site investigation for PCBs in soil samples.	construction:							
		Conduct further site investigation for PAH, Dioxins and Metals	Existing							
		(Cr, Co, Ni, Cu, Zn, As, Mo, Cd, Sn, Ba, Hg, Pb) in soil samples.	crematorium:							
		(61) 60) 111, 64, 211, 110, 110, 64, 611, 24, 115, 11 0011 04111 0611	Dangerous							
			goods store,							
			Daily tank							
			room, fuel pump room and							
			sunken fuel							
			pipe							
			Skeletal							
			Cremator							
			Building:							
1			Dangerous							
			goods store Existing							
			crematorium:							
			Transformer							
			room							
			Cremators							
			(residual inside							
			the cremator,							
			flue and							



EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
			chimneys				
	nagemer	nt (Construction Phase)		T			_
S.6.7.24		Good Site Practice: ■ Obtain the necessary waste disposal permits from the appropriate authorities, if they are required, in accordance with the Waste Disposal Ordinance (Cap. 354), Waste Disposal (Chemical Waste) (General) Regulation and the Land (Miscellaneous Provision) Ordinance (Cap. 28). ■ Obtain a billing account with EPD for disposal of construction waste. ■ A Waste Management Plan (WMP), incorporated in an Environmental Management Plan (EMP) shall be prepared and submitted to the Engineer/Supervising Officer for approval. Reference shall be made to Environment, Transport and Works Bureau Technical Circular (Works) (ETWB TCW) 19/2005.	Project site/ design, construction and demolition stages	Contractor	Construction Phase	Waste Disposal Ordinance (Cap. 354) Waste Disposal (Chemical Waste) (General) Regulation Waste Disposal (Charges for Disposal of Construction Waste) Regulation	Implemented and rectified according to observation
		 Nomination of an approved person to be responsible for good site practice, arrangements for collection and effective disposal to an appropriate facility of all wastes generated at the site. Use of a waste haulier, authorised or licensed to collect specific category of waste. A trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team to monitor the disposal of C&D and solid wastes at public filling facilities and landfills, and to control fly tipping. Reference shall be made to ETWB TCW No. 31/2004. 					
		 Training of site personnel in proper waste management and chemicalwaste handling procedures. Separation of chemical wastes for special handling and appropriate treatment at a licensed facility. Routine cleaning and maintenance programme for drainage systems, sumps and oil interceptors. Provision of sufficient waste disposal points and regular collection for disposal. Adoption of appropriate measures to minimise windblown litter and dustduring transportation of waste, such as covering trucks or transporting wastes in enclosed containers. Implementation of a recording system for the amount of wastes 					



EIA Ref Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
	generated, recycled and disposed of (including the disposal sites).					
S.6.7.25	 Waste Reduction Measures: Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal. Encourage collection of aluminium cans, plastic bottles and packaging material (e.g. carton boxes) and office paper by individual collectors. Separate labelled bins shall be provided to help segregate this waste from other general refuse generated by the work force. Any unused chemicals or those with remaining functional capacity shallbe recycled as far as practicable. Reuse C&D materials when possible to reduce the amount of C&D material/waste. Wood, steel and other metals shall be separated for reuse and / or recycling Prior to disposal of C&D waste to minimise the quantity of waste to be disposed of to landfill. Minimise the potential for damage or contamination of construction material by having proper storage and site practices. Plan and stock construction materials carefully to minimise the amount of waste generated. 	Project site / construction and demolition stages	Contractor	Construction Phase	WBTC No. 32/1992 WBTC No. 19/2005	Implemented



	<u> </u>	erry aman report no.0		1			
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.6.7.4		Excavated Material Rock and soil generated from excavation shall be reused for site formation and excavated material from foundation work reused for landscaping as far as practicable to avoid disposal off-site.	Project site / construction and demolition stages	Contractor	Construction Phase	WBTC No. 12/2000	Implemented
S.6.7.5	S.5.3.5	Construction and Demolition Material	Project site /	ArchSD /	Construction Phase	WBTC No. 2/93	Implemented
S.6.7.7	S.5.3.9	 Reuse of the public fill and C&D waste shall be practiced on site as faras practicable. The handling of C&D materials is governed by WBTC No. 2/93. Inert C&D material (public fill) shall be directed to an approved public filling area or reclamation site, where it has the benefit of offsetting the need for removal of materials from borrow areas for reclamation purposes and helps to reduce the pressure on landfill sites. Individuals or companies who deliver public fill to public filling areas require dumping licences. Careful design, planning and good site management can minimise over- ordering and generation of waste materials such as concrete, mortar and cement grouts. The design of formwork shall maximise the use of standard wooden or metal panels so that high reuse levels can be achieved. Alternatives such as steel formwork, plastic fencing and reusable site office structures shall be considered to 	construction and demolition stages	Contractor		The Land (Miscellaneous Provision) Ordinance WBTC No. 19/2005	Impremented
		 increase the potential for reuse and minimise C&D waste generation. ■ The contractor shall use as much as possible of the C&D material onsite. Proper segregation of waste types on site will increase the feasibility of certain components of the waste stream by recycling contractors. 					



	_	erry Errecrittepe								
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures				Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.6.11.1 - S.6.11.5	S.5.3.1 0 - S.5.3.1 4	3.1	Cremators, Flues Chimneys and surrounding areas / After	FEHD, ArchSD, Contractor	Construction Phase	ProPECC PN 2/97 ProPECC PN 3/94 APCO	NA			
		Crematorium, the following further contamination investigations shall be carried out to confirm the quality and quantity of ash waste and building structures requiring treatment and disposal.			decommissioni ng but prior to demolition of the existing crematorium.					
		Location	Investigatio n Parameter	Investigatio n Period	Responsible Party	sible				
		Cremators / flue / chimney and surround ing areas	Asbestos (building structures)	After decommissionin g but prior to demolition of the Existing	The Contractor					
		Cremators / flue / chimney and surrounding areas	Dioxins, heavy metals, PAH (ash waste)	Crematorium						
		 Prior to any demolition work commencing, these areas suspected to contain asbestos containing material (ACM) shall be further inspected by aregistered asbestos consultant to determine the presence of any ACM. These areas shall be thoroughly investigated and the additional findings submitted as supplementary information to the Asbestos Investigation Report. Samples shall be analysed for the presence and type of asbestos according to the Laboratory's HOKLAS accredited testing procedures. If the findings of the investigation indicate ACM materials present on the premises an Asbestos Abatement Plan 								
				s an Asbestos Abate encement of demolit						



EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
		■ It is not currently possible to conduct inspection and sampling within the cremators, chimney and flues to assess the levels of contamination due to the operation of the crematorium. It is recommended that samples shall be collected from the potential areas of contamination for testing of dioxin, heavy metal and PAH after decommissioning and prior to the demolition of the Existing Crematorium.					
S.6.9.6 - S.6.9.7	S.5.3.1 5 - S.5.3.1 7	 Asbestos Containing Material Asbestos wastes shall be handled in accordance with the Code of Practice on the Handling, Transportation and Disposal of Asbestos Waste issued by the Environment and Food Bureau. Production, collection and disposal of Asbestos waste will follow the 'trip-ticket' system. The registered asbestos contractor shall appoint a licensed asbestos waste collector to collect the packaged asbestos waste and deliver it to the designated landfill for disposal. Notification has to be given to EPD for its disposal. EPD will normally require ten working days notice of the intention to dispose of any quantity of asbestos waste. After processing the notification, EPD will issue specific instructions and directions for disposal of the waste. The waste producer or agent must strictly follow these directions. 	Cremator room in Existing Crematorium / before demolition and after decommission	Contractor	Construction Phase	COP on Handling, Transportation and Disposal of Asbestos Waste under the Waste Disposal (Chemical Waste) (General) Regulation.	NA
		Dioxin Contaminated Materials (DCM) / Heavy Metal Contaminated Materials (HMCM) / Polyaromatic Hydrocarbon Contaminated Materials (PAHCM) from Demolition of the Existing Crematorium Proposed Contamination Classifications for Ash Waste with DCM / HMCM / PAHCM.	Cremator room in Existing Crematorium / before demolition and after decommission	Contractor	Construction Phase	ProPECC PN 3/94 APCO	NA



	Q 0.0.7 0.	city EMEAT Report No.0							
EIA Ref	EM&A Ref.	Environmental Protecti	ion Measures / M	litigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
		Classification of Contamination	Dioxin Level in ash waste	Heavy Metal Level / Polyaromatic Hydrocarbon in Ash Waste					
		Low Contaminated DCM/HMCM/PAHCM	<1 ppb TEQ	< Dutch "B" List					
		Moderately/Severely Contaminated HMCM/PAHCM	<1 ppb TEQ	> Dutch "B" List					
		Moderately Contaminated DCM	> 1 and < 10 ppb TEQ	Any Level					
		Severely contaminated DCM	>10 ppbTEQ	Any Level					
S.6.9.9	S.5.3.1 9	Demolition, Handling, Treats DCM / HMCM / PAHCM fron			Cremator room in Existing Crematorium / demolition	Contractor	Construction Phase	ProPECC PN 3/94 APCO	NA
		■ Where the ash waste cont PAHCM, the contractor sh during demolition. Genera followed. The ash waste co	all avoid ash waste l al dust suppression	becoming airborne measures shall be					
S.6.9.10 - S.6.9.14	S.5.3.2 0 - S.5.3.2 4	Demolition, Handling, Treati Severely Contaminated DCM Contaminated HMCM / PAH Crematorium Site preparation procedures:	I and Moderately / S CM from Demolition	Severely	Cremator room in Existing Crematorium / demolition	Contractor	Construction Phase	Waste Disposal (Chemical Waste) (General) Regulation ProPECC PN 3/94	NA
		■ Except the cremators/flue items shallbe removed as decontamination activities	far as practicable to					APCO	
		Preliminary site decontant using High Efficiency Part	iculate Air (HEPA) v	acuum cleaner.					
		■ A chamber with three laye	ers of polythene she	ets shall enclose the					



	Ť	7					
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
		top portion of the chimney above the roof.					
		■ A 3-chamber decontamination unit shall be constructed at the entrance to the cremators/flues/chimney for entry and exit from the work area. It shall comprise a dirty room, a shower room and a clean room of at least 1m x 1m base with 3 layers of fire retardant polythene sheet.					
		■ Workers shall carry out decontamination procedures before leaving thework area.					
		All workers shall wear full protective equipment, disposable protective overall, nitrile gloves, rubber boots, and full-face positive pressure respirator.					
		Warning signs in both Chinese and English shall be put up in conspicuous areas.					
		Site preparation procedures specific to severely contaminated DCM:					
		■ The walls, floor and ceiling of the cremator room shall be lined with 3-layers of fire retardant polythene sheets.					
		■ Air movers shall be installed at the cremator room, and at the bottom of the chimney to exhaust air from the work area. A stand by air mover shall also be installed with each of the air movers. Sufficient air movement shall be maintained to give a minimum of 6 air changes per hour to the work area.					
		New pre-filters and HEPA filters shall be used on the air movers.					
		■ Before commencement of the decommissioning work a smoke test with non-toxic smoke shall be carried out to ensure the air tightness of the containment.					
		Demolition and handling procedures:					
		■ The cremators/flue/chimney shall be removed from top down.					
		■ Scrubbing and HEPA vacuuming shall be used to remove any ash or residues attached to the cremators, flue, chimney and other building structures.					
		■ Wastes generated from the contaminant or decontamination unit including the workers protection clothing shall be disposed of at landfill site.					
		After completion of removal, all surfaces shall be decontaminated by HEPA vacuum.					
		■ If any contaminated wastewater needs to be discharged out of the					



		J P					
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
		site, it shall be properly treated to WPCO requirements with prior agreements with EPDon discharge standards.					
		Demolition and handling procedures specific to severely contaminated DCM:					
		■ The contaminated detached sections of the building structures shall be wrapped with 2 layers of fire retardant polythene sheets. A third layer shall be wrapped and secured with duct tape. Wet wiping shall be used to decontaminate the outer layer.					
		■ After completion of removal and decontamination, spray the innermost layer of the fire retardant polythene sheet with PVA. Upon drying, peel off and dispose of at landfill site. Repeat for the other 2 layers disposing the final layer as contaminated wastes.					
		Treatment and disposal procedures:					
		■ Immobilise the ash waste by mixing with cement in the correct ratio as determined by pilot mixing and TCLP test.					
		■ Place material in polythene lined steel drums for disposal at landfill. The drums should clearly be marked with "DANGEROUS CHEMICAL WASTE" in English and Chinese. Prior agreement of the disposal criteria must be obtained from EPD and the landfill operator.					
		If the landfill disposal criteria cannot be met, disposal at the CWTC in TsingYi shall be considered.					
S.6.9.1	S.5.3.2	Chemical Waste	Project site /	Contractor	Construction Phase	Code of Practice on the	Implemented
S.6.9.2	5 -	■ Should any chemical waste be generated, the Contractor must registerwith the EPD as chemical waste producer.	demolition			Packaging, Labelling and Storage of	
	S.5.3.7	■ All the chemical waste shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. The chemical waste shall be stored and collected by an approved contractor for disposalat a licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.				Chemical Wastes Waste Disposal (Chemical Waste)	
		■ Principles of reuse and recycle chemical waste on site as far as practicable shall be adopted by the Contractor.				(General) Regulation.	



	C	ing international internationa					
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.6.9.3	S.5.3.2	Containers used for the storage of chemical waste shall:					
	8	■ Be suitable for the substance they are holding, resistant to corrosion, maintained in good condition, and securely closed.					
		■ Have a capacity of less than 450 litres unless the specifications have been approved by the EPD.					
		■ Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Waste Disposal (Chemical Waste) (General) Regulation.					
S.6.9.4	S.5.3.2	The storage area for chemical waste shall:					
	9	■ Be clearly labelled and used solely for the storage of chemical waste.					
		■ Be enclosed on at least 3 sides.					
		■ Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.					
		■ Have adequate ventilation.					
		■ Be covered to prevent rainfall entering (water collected within the bundmust be tested and disposed as chemical waste if necessary).					
		■ Be properly arranged so that incompatible materials are adequately separated.					
S.6.9.25	S.5.3.3	Disposal of chemical waste shall be:					
	0	■ Via a licensed waste collector.					
		■ A facility licensed to receive chemical waste, such as the Chemical Waste Treatment Facility at Tsing Yi, which offers a chemical waste collection service and can supply the necessary storage containers. or					
		■ A waste recycling plant approved by EPD.					



	Quart.	Try Linear report No.0					
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.6.7.27 - S.6.7.28	S.5.3.3 1 S5.3.3 2	 General Refuse General refuse shall be stored in enclosed bins or compaction units separate from C&D and chemical wastes. A reputable waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D and chemical wastes, on a daily or every second day basis to minimise odour, pest and litter impacts. Individual collectors often recover aluminium cans from the waste stream if they are segregated or easily accessible. Therefore, separately labelled bins for their deposit shall be provided if feasible. Similarly, plastic bottles and carton package material generated on site shall be separated for recycling as far as possible. Site office waste shall be reduced through recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme shall be considered if one is available. 	Project site / construction and demolition stages	Contractor	Construction Phase		Implemented
Waste Ma	anageme	ent (EM&A)					
S.11.2.17		Supplementary site investigations shall be conducted for asbestos in building structures and for dioxins, heavy metals and PAH in ash/particular matter samples.	Cremators / flue / chimney and surrounding area. After decommissioni ng but prior to demolition	Contractor	Construction Phase	ProPECC PN 2/97 and 3/94 AIR, AMP/AAP to be submitted under APCO Future Supplementary Investigation Site Plan	NA
Landscap	e and Vi	sual (Construction Phase)					
S.7.9.2 MC 1	S.6.3.1	 Site offices and construction yards: Site offices shall have olive green roof and façade coating or colour matches with existing environment. Site offices and the construction yard shall be decommissioned after construction. 	All site offices / Design and construction phases	ArchSD's Contractor	Construction Phase		Implemented
S.7.9.2 MC 2	S.6.3.1	Height of site offices: The height of site offices, including the rooftop shall not exceed 10m. Building services equipment such as antennas may exceed 10m and shall be coated in black.	All site offices / Design and construction phases	ArchSD's Contractor	Construction Phase		Implemented



EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.7.9.2 MC 3	S.6.3.1	Hoarding and screening: Where practical the site offices areas, construction yards and storage areas shall be screened using colour in harmony with the surrounding environment around the peripheries of the works area until the completion of relevant construction phases.	All site offices and construction yard areas / Design and construction phases	ArchSD's Contractor	Construction Phase		Implemented
S.7.9.2 MC 4	S.6.3.1	 Construction plant and building material: Shall be orderly and carefully stored in order to appear neat and avoid visibility from outside where practical. Excess materials shall be removed from site as soon as practical. All construction plants shall be removed from site upon completion of construction works. 	Works site / Design and construction phases	ArchSD's Contractor	Construction Phase		Implemented
S.7.9.2 MC 5	S.6.3.1	Construction light: To be oriented away from the viewing location of VSRs. All lighting facing sensitive receiver shall have frosted diffusers and reflective covers.	All construction lights / Design and construction phases	ArchSD's Contractor	Construction Phase		Implemented
S.7.9.2 MC 6	S.6.3.1	Silting trap: Silting traps shall be installed to minimise silting to streams.	Streams / Construction phase	Contractor	Construction Phase		NA
S.7.9.3 MT 1	S.6.3.1	Compensation for losses: The tree compensation to tree loss ratio shall be at least 1:1 in term of quantity.	Within the Wo Hop Shek Crematorium	ArchSD's Contractor	Construction Phase	ETWB TCW No. 2/2004 ETWB TCW No. 3/2006	NA
S.7.9.3 MT 2	S.6.3.1	Where practical, trees that require removal shall be transplanted on Site.	Work site / Design and construction phases	ArchSD's Contractor	Construction Phase	ETWB TCW No. 2/2004 ETWB TCW No. 3/2006	Implemented



		y v v v v					
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.7.9.3 MT 3	S.6.3.1	 Amenity planting: Planting works shall be carried out under the supervision of a specialist landscape sub-contractor. The rooftop of the cremation plant room shall be planted with lawn. Open spaces shall be included Project. Screen planting such as planting a roll of trees along the site boundary butting Kiu Tau Road shall be carried out. New trees, shrubs and groundcover shall be carefully selected and 	As shown on mitigation measure plans / All phases	ArchSD's & FEHD's Contractor	Construction Phase	ETWB 2/2004	NA
S.7.9.3 MT 4	S.6.3.1	designed to homogenize with the environment. Woodland mix planting: Woodland mix, comprising of tree seedlings and shrubs, shall be planted within the Wo Hop Shek Cemetery to enhance the ecological value and compensatory of tree loss.	Within the Wo Hop Shek Cemetery / All phases	ArchSD's Contractor	Construction Phase	ETWB TCW No. 2/2004ETWB TCW No. 3/2006	NA
S.7.9.3 MT 5	S.6.3.1	Preservation: No tree shall be transplanted or felled without prior approval by relevant Government departments. All trees that are marked for retention shall be fenced off with a 1.2mhigh fence around the dripline of trees or larger area as far as feasible. Transplant preparation works shall be carried as soon as possible after commencement of construction. Over-pruning such as hard pruning of tree crown, pollarding or topping shall be avoided. Rootball and crown pruning shall be carried out over at least 3 months. Existing shrub and ground cover planting areas that will not be removed shall be maintained in good condition and enhanced where practical.	Work site / All phases	ArchSD's Contractor	Construction Phase	ETWB TCW No. 2/2004 ETWB TCW No.	Implemented
S.7.9.4 MB 1	S.6.3.1	The 10m height headroom cremation plant room shall be half sunken to reduce the visual impact to pedestrians.	Cremation plant room / Design phase	ArchSD's Contractor	Construction Phase		NA
S.7.9.4 MB 2	S.6.3.1	The chimney shall be designed to have sculptural outlook and articulated.	Chimney / Design phase	ArchSD's Contractor	Construction Phase		NA
S.7.9.4 MB 3:	S.6.3.1	The chimney stacks shall be designed to locate at the least conspicuous location of the site to VSRs.	Chimney / Design phase	ArchSD's Contractor	Construction Phase		NA
Landscap	e and V	isual (EM&A)					



	_	<i>y</i> 1					
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.11.2.23	S.6.2	Details of the inspection frequency and parameters will be outlined in the EM&A Manual.	Work site / Construction	Contractor	Construction Phase		NA
S.11.2.24	alita (C.	an atmosti an Dhaga)					
		onstruction Phase) Construction Runoff and Drainage	Moule aite /	Combination	Construction Phase	ProPECC PN 1-	Immlemented
S.8.7.1	S.7.2.2	<u> </u>	Work site / Construction	Contractor	Constituction Filase	94 & WPCO	Implemented
S.8.7.4		Wastewater shall be properly treated to meet the discharge standards set out in the relevant Water Pollution Control Ordinance (WPCO) discharge licence. No direct discharge of site runoff into the two streams shall be allowed.	Construction			94 & WFG0	
		■ Provision of perimeter channels to intercept storm runoff from outside the Site. These shall be constructed in advance of site formation works andearthworks.					
		■ Sand/silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove sand/silt particles from runoff to meet the requirements of the Technical Memorandum standard under the WPCO.					
		■ Works shall be carefully programmed to minimise soil excavation works during rainy seasons.					
		Exposed soil surface shall be protected by paving as soon as possible to reduce the potential of soil erosion.					
		■ Temporary access roads shall be protected by crushed gravel and exposed slope surfaces shall be protected when rainstorms are likely to occur.					
		■ Trench excavation shall be avoided in the wet season as far as practicable, and if necessary, these trenches shall be excavated and backfilled in short sections.					
		Open stockpiles of construction materials on Site shall be covered with tarpaulin or similar fabric during rainstorms.					
		■ Sand and silt in the wash water from the wheel from the wheel washing facility shall be settled out and removed before discharging into the storm drain.					
		■ Oil receptor shall be provided in the drainage system and regularly emptied to prevent the release of oil and grease into the storm drainage system after accidental spillage.					



EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
S.8.7.5	S.7.2.3	 General Construction Activities Debris and rubbish generated on Site shall be collected, handled and disposed of properly to avoid them entering the two streams. All fuel tanks and storage areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. Open storm water drains and culverts near the works area shall be 	Work site / Construction phase	Contractor	Construction Phase	ProPECC PN 1- 94 & WPCO	Implemented
S.8.7.6	S.7.2.4	covered to block the entrance of large debris and refuse. Sewage from On-site Workforce: Portable chemical toilets shall handle the sewage from construction work force if the existing toilets in the Site are not adequate. Licensed contractors who shall be responsible for appropriate disposal and maintenance of these facilities shall provide appropriate and adequate portable toilets. Sheet piling shall be provided at suitable location around the basement excavation to reduce the effect of lowering the water table from any dewatering process. Any discharge of groundwater pumped out from any dewatering process of the construction works shall be treated to comply with the standards set in the relevant discharge licence prior discharge. No discharge of the groundwater shall be allowed into the two streams.	Work site / Construction phase	Contractor	Construction Phase	WPCO	Implemented
Ecology (S.9.8.3 -		 Mitigation to minimise impacts on habitat and vegetation loss: Layout of the Project shall be carefully designed to avoid or minimise thearea of habitat loss and the numbers to trees to be felled. All trees shall be preserved as far as possible, especially species of conservation concern. Recommendations to be provided in the Tree Survey Report to mitigate impacts on trees shall be followed. Disturbance of individuals of the shrub / tree Transplantation of the two shrub / tree species of conservation concern, namely Aquilaria sinensis and Cibotium barometz, shall be avoided. Where loss of these species would be unavoidable, it is recommended to transplant them to same habitats with similar conditions. Following transplantation, regular monitoring of these trees shall be conducted by a suitable qualified botanist / horticulturist over a 12- 	Work site particularly semi- natural woodland / Design and construction phases.	Arch SD / Contractor	Construction Phase	ETWB Technical Circular No. 3/2006	Implemented



	Q 0.0.7 C	Try Linear report No.0				100000000000000000000000000000000000000	
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
		month period. Transplantation of any affected trees to grassland / scrubland within theWo Hop Shek Cemetery. Compensatory planting of the felled trees shall follow the Technical Circular No. 3/2006 issued by ETWB.					
S.9.8.15 - S.9.8.16	S.8.3.1	Mitigation to construction runoff through general good site practice:	Work site / Construction phase	Contractor	Construction Phase	ETWB Technical Circular (Works) No. 5/2005.	Implemented
		■ Temporary access to the work sites shall be carefully planned and located to minimise disturbance caused to the streams and nearby habitats.					
		Use of less or smaller construction plant may be specified toreduce disturbance to the streams and nearby habitats.					
		■ Temporary sewage system shall be designed and installed to collect wastewater and prevent it from entering the streams and nearbyhabitats.					
		■ The Site inside or in the proximity of the streams and nearby habitats shallbe temporarily isolated, such as by placing of sandbags or silt curtains with lead edge at bottom and properly supported props, to prevent adverse impacts on these areas.					
		■ Natural bottom and existing flow in the streams shall be preserved as muchas possible to avoid disturbance to the stream habitats.					
		■ Proper locations well away from the streams and nearby habitats for temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction debris and spoil shall be identified before commencement of the works.					
		■ Stockpiling of construction materials, if necessary, shall be properly covered and located away from the streams and nearby habitats.					
		■ Construction debris and spoil shall be covered up and/or properly disposed of as soon as possible to avoid being washed into the streams and nearby habitats by rain.					
		■ Construction effluent, site runoff and sewage shall be properly collected and/or treated.					



	Quarterly Liver Report 10.0						
EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
		■ Proper locations for discharge outlets of wastewater treatment facilities well away from the streams and nearby habitats shall be identified.					
		■ Vehicles and other plant shall be carefully maintained and properly used to minimise the chance for accidental spillage.					
		Any spillages that do occur shall be quickly identified and appropriately cleaned up before they can contaminate streams or groundwater.					
		■ Temporary geo-textile silt fences around earth moving works shall beerected to trap any sediments being washed away and prevent them from entering surrounding areas.					
		■ Silt traps shall be installed at points where drainage from the Site enters temporary sewage system.					
		Exposed soil or other loose materials shall be covered with tarpaulins to prevent erosion, and then seeded and covered with a biodegradable geo- textile blanket for erosion control purposes.					
S.9.8.18		Mitigation to protect the groundwater:	Work site /	Contractor	Construction Phase		NA
		■ Basement formation or any construction activities likely to pump out a large quantity of groundwater shall be protected with sheet-piling at suitable locations around the basement footprint, or by any like method.	Construction phase				
		■ No groundwater shall be pumped back to the two stream courses to protect the natural integrity of the stream habitat and the associated organism.					
S.9.8.20	S.8.3.1	Mitigation for noise and other disturbance on ecological integrity:	Work site /	Contractor	Construction Phase		Implemented
		■ Use of sturdy 1.8 metres protective fencing shall be located at the edge of the tree canopy but not around the trunk.	Construction phase				
		■ Works beneath the tree canopy shall be avoided: If encroachment under the canopy area is unavoidable, adequate protections shall be provided to ensure no damage of any part of the tree would occur due to the encroachment.					
		■ An approved Landscape Contractor shall implement any tree transplanting and planting works. Quality control of the work shall be undertaken by a qualified Landscape Architect through site inspections and approval of works.					



EIA Ref	EM&A Ref.	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stage	Relevant Legislation and Guidelines	Implementation Status
		■ Construction works shall be restricted to works area which are clearly defined.					
		Woodland or other habitats that would be affected by the constructionworks shall be well-defined and minimised.					
		■ Human inference to habitats beyond the site boundary and habitats proposed to be retained shall be avoided by providing temporary barricades.					
		Works area shall be reinstated immediately after completion of the construction.					
		■ Waste and other garbage generated during the construction of the proposed development shall be dumped properly.					
		Uncontrolled fire shall be strictly prohibited. Appropriate fire control measures shall be provided in order to protect nearby habitats.					
Ecology (EM&A)						
S.9.11	S.8.2.1	Audit/Inspection:	Work site /	Contractor	Construction Phase		Implemented
&		■ Regular site audit / inspection shall be conducted at least once a	Construction				
S.11.2.29		week to inspect the implementation of the recommended mitigation measures (details to be outlined in the EM&A Manual).	phase				
S.11.2.32	S.8.2.2	Monitoring on Transplantation:	Work site /	Contractor	Construction Phase		Implemented
S.11.2.33	S.8.2.4	■ Trees requiring transplantation or protection shall be identified based on the information illustrated in the Tree Survey Report.	Construction phase				
		Regular monitoring after transplantation of Aquilaria sinensis and Cibotium barometz individuals shall be conducted to check on the health and conditions of the plants. Monitoring shall cover the 12-month period following transplantation. The monitoring shall be conducted by a suitably qualified botanist / horticulturist at least twice a month for the first four months after transplantation, and once a month for the remaining eight months.					



APPENDIX D: IMPACT MONITORING SCHEDULE OF THE REPORTING PERIOD



Impact Monitoring Schedule for Expansion of Wo Hop Shek Crematorium						
Jul-21						
Sun	Mon	Tue	Wed			Sat
				1	2	3
4	5	6	7	8	9	10
	Air monitoring for A10, A20 for 1- hr TSP and 24-hr TSP Monitoring Time: 0900-1630				Weekly ET site inspection and audit	Air monitoring for A10, A20 for 1- hr TSP and 24-hr TSP Monitoring Time: 0900-1630
11	12	13	14	15	16	17
			Weekly ET site inspection and audit		Air monitoring for A10, A20 for 1- hr TSP and 24-hr TSP Monitoring Time: 0900-1630	
18	19	20	21	22	23	24
			Weekly ET site inspection and audit	Air monitoring for A10, A20 for 1- hr TSP and 24-hr TSP Monitoring Time: 0900-1630		
25	26	27	28	29	30	31
			Weekly ET site inspection and audit Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630			

^{*}Remarks: 1. This impact monitoring schedule is subject to change due to adverse weather conditions or other rationales.

^{2.} Advance notification of the changes will be given to all relevant parties at lease 48 hours prior to implementation.



	Impact Monitoring Schedule for Expansion of Wo Hop Shek Crematorium						
	Aug-21						
Sun	Mon		Wed 4		Fri 6	Sat 7	
		Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630	~			,	
8	9	10	11	12	13	14	
	Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630	Weekly ET site inspection and audit				Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630	
15	16	17	18	19	20	21	
			Weekly ET site inspection and audit		Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630		
22	23	24	25	26	27	28	
			Weekly ET site inspection and audit	Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630			
29	30	31					

^{*}Remarks: 1. This impact monitoring schedule is subject to change due to adverse weather conditions or other rationales.

^{2.} Advance notification of the changes will be given to all relevant parties at lease 48 hours prior to implementation.



Impact Monitoring Schedule for Expansion of Wo Hop Shek Crematorium						
Sep-21						
Sun	Mon	Tue	Wed	Thur		Sat 4
			Weekly ET site inspection and audit Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630		3	
5	6	7	8	9	10	11
		Weekly ET site inspection and audit Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630				
12	13	14	15	16	17	18
	Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630		Weekly ET site inspection and audit			Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630
19	20	21	22	23	24	25
				Weekly ET site inspection and audit	Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630	
26	27	28	29	30		
			Weekly ET site inspection and audit Air monitoring for A10, A20 for 1-hr TSP and 24-hr TSP Monitoring Time: 0900-1630			

^{*}Remarks: 1. This impact monitoring schedule is subject to change due to adverse weather conditions or other rationales.

^{2.} Advance notification of the changes will be given to all relevant parties at lease 48 hours prior to implementation.



APPENDIX E: EVENT/ACTION PLAN FOR DUST EXCEEDANCE



Evant	Action						
Event	ET	IEC	AR	Contractor			
Action Level							
Exceedance for one sample 2. Exceedance for	 Identify source, investigate the causes of complaint and propose remedial measures; Inform IEC and AR; Repeat measurement to confirm finding; Increase monitoring frequency to daily. Identify source; 	 Check monitoring data submitted by ET; Check Contractor's working method. Check monitoring data 	Notify Contractor. Confirm receipt of	 Rectify any unacceptable practice; Amend working methods if appropriate. Submit proposals for 			
two or more consecutive samples	 Identify source; Inform IEC and AR; Advise the AR on the effectiveness of the proposed remedial measures; Repeat measurements to confirm findings; Increase monitoring frequency to daily; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with IEC and AR; 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Supervise Implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Notify Contractor; Ensure remedial measures properly implemented. 	 Submit proposals for remedial to AR within three working days of notification; Implement the agreed proposals; Amend proposal if appropriate. 			



Event	Action						
Event	ET	IEC	AR	Contractor			
	8. If exceedance stops, cease additional monitoring.						
Limit Level							
1. Exceedance for one sample	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC, AR, Contractor and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and AR informed of the results. 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the AR on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Notify Contractor; Ensure remedial measures properly implemented. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within three working days of notification; Implement the agreed proposals; Amend proposal if appropriate. 			
2. Exceedance for two or more consecutive samples	 Notify IEC, AR, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working 	 Discuss amongst AR, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the AR accordingly; 	 Confirm receipt of notification of exceedance in writing; Notify Contractor; In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within three working days of notification; Implement the agreed proposals; 			




Event	Action						
Event	ET	IEC	AR	Contractor			
	procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and AR to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and AR informed of the results; 8. If exceedance stops, cease additional monitoring.	3. Supervise the implementation of remedial measures.	 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the AR until the exceedance is abated. 			



APPENDIX F: LOCATION PLAN OF AIR QUALITY MONITORING STATION



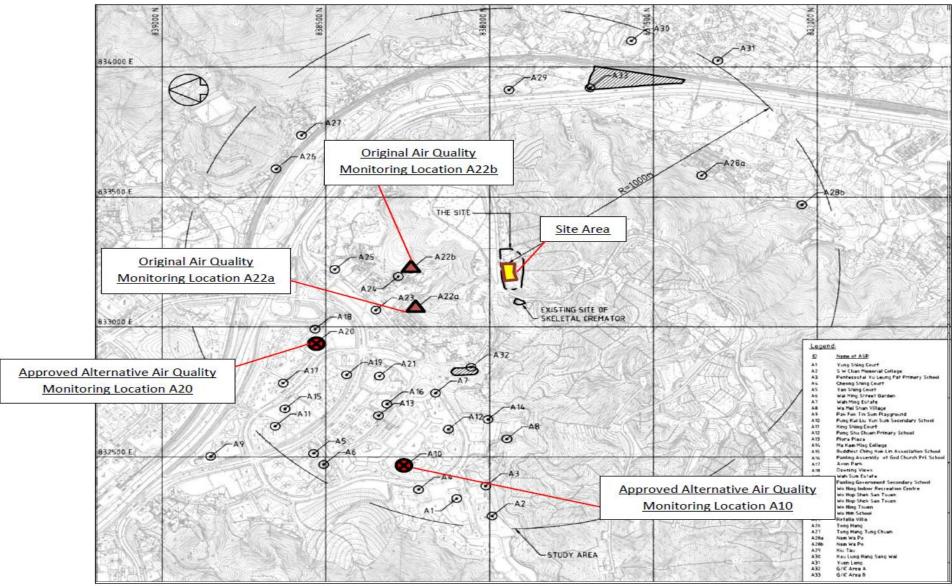



APPENDIX G: AIR QUALITY MONITORING DATA



The Summary of 1-hour TSP Concentration ($\mu g/m^3$) at A10


		The Julillia	ly of I flour I	51 Concentrat	ion (μg/m³) at	ALU		
Date	Weather	Sampling Time (1)	Sampling Time (2)	Sampling Time (3)	Reading (1) μg/m³	Reading (2) μg/m³	Reading (3) μg/m ³	Average μg/m³
5/7/2021	Sunny	10:20	11:20	12:20	47	52	50	50
10/7/2021	Sunny	9:52	10:52	11:52	43	49	48	47
16/7/2021	Sunny	10:23	11:23	12:23	42	40	47	43
22/7/2021	Sunny	10:24	11:24	12:24	40	44	44	43
28/7/2021	Sunny	10:29	11:29	12:29	48	53	49	50
3/8/2021	Sunny	10:21	11:21	12:21	49	44	45	46
9/8/2021	Fine	10:20	11:20	12:20	47	53	46	49
14/8/2021	Cloudy	09:41	10:41	11:41	42	48	47	46
20/8/2021	Fine	13:50	14:50	15:50	41	45	50	45
26/8/2021	Sunny	11:01	12:01	13:01	51	42	41	45
1/9/2021	Cloudy	10:47	11:47	12:47	46	48	43	46
7/9/2021	Sunny	10:14	11:14	12:14	44	49	49	47
13/9/2021	Sunny	10:17	11:17	12:17	52	58	61	57
18/9/2021	Sunny	10:20	11:20	12:20	46	51	51	49
24/9/2021	Fine	11:01	12:01	13:01	56	57	61	58
29/9/2021	Fine	10:35	11:35	12:35	51	58	60	56

Average 1-hour TSP: 49

Max.: 61

Min.: 40



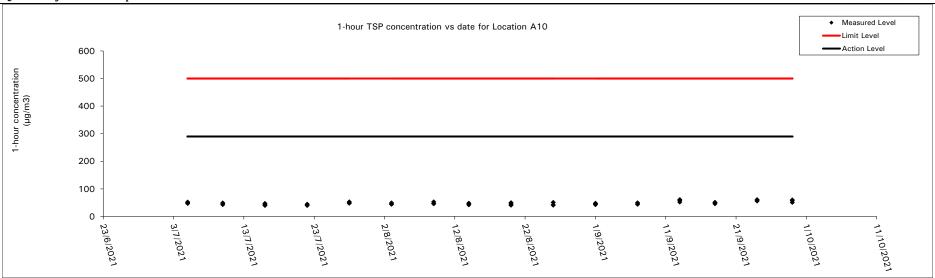



The Summary of 1-hour TSP Concentration (μg/m³) at A20


		THE Julillia	ny or 1-nour 1	or concentrat	ion (μg/m³) at	. ALU		
Date	Weather	Sampling Time (1)	Sampling Time (2)	Sampling Time (3)	Reading (1) μg/m³	Reading (2) μg/m³	Reading (3) μg/m³	Average μg/m³
5/7/2021	Sunny	10:58	11:58	12:58	59	51	55	55
10/7/2021	Sunny	10:24	11:24	12:24	52	55	49	52
16/7/2021	Sunny	10:59	11:59	12:59	44	48	51	48
22/7/2021	Sunny	10:54	11:54	12:54	48	53	47	49
28/7/2021	Sunny	11:00	12:00	13:00	52	59	59	57
3/8/2021	Sunny	10:59	11:59	12:59	53	49	56	53
9/8/2021	Fine	10:47	11:47	12:47	54	50	55	53
14/8/2021	Cloudy	10:09	11:09	12:09	47	48	51	49
20/8/2021	Fine	13:18	14:18	15:18	50	41	43	45
26/8/2021	Sunny	11:37	12:37	13:37	43	47	48	46
1/9/2021	Cloudy	11:28	12:28	13:28	51	46	44	47
7/9/2021	Sunny	9:30	10:30	11:30	46	53	55	51
13/9/2021	Sunny	09:25	10:25	11:25	55	62	66	61
18/9/2021	Sunny	09:47	10:47	11:47	49	52	57	53
24/9/2021	Fine	11:42	12:42	13:42	47	57	46	50
29/9/2021	Fine	9:45	10:45	11:45	53	58	59	57

Average 1-hour TSP: 52

Max.: 66

Min.: 41



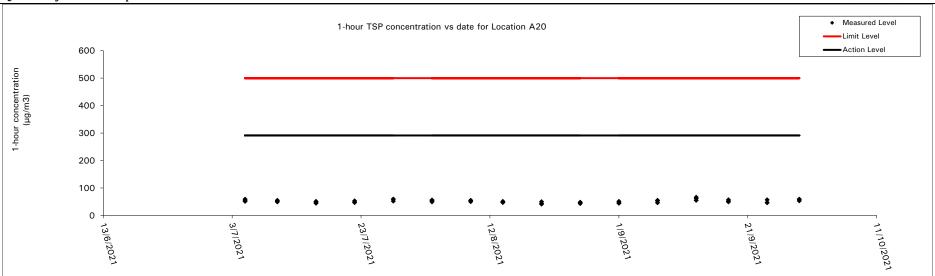



Start Date	Weather	Weather Elapse Time Condition		ie	Chart Reading		Avg Air Temp	Avg Atmospheric Pressure	Flow Rate	Standard Air Volume		Weight g)	Particulate weight	Conc.	
	Condition	Initial	Final	Actual (min)	Min	Max	Avg	(°C)	(mm Hg)	(m³/min)	(m³)	Initial	Final	(g)	(μg/m³)
05/07/2021	Sunny	7518.7	7542.7	1440.0	39	39	39.0	30.2	755.6	1.26	1815	2.7368	2.7760	0.0392	22
10/07/2021	Sunny	7542.7	7566.7	1440.0	39	40	39.5	30.5	757.8	1.31	1882	2.7625	2.8001	0.0376	20
16/07/2021	Sunny	7567.1	7591.1	1440.0	39	39	39.0	29.6	756.4	1.21	1745	2.7438	2.7861	0.0423	24
22/07/2021	Sunny	7591.1	7615.1	1440.0	39	39	39.0	29.3	750.8	1.19	1715	2.7247	2.7789	0.0542	32
28/07/2021	Sunny	7615.1	7639.1	1440.0	39	40	39.5	30.8	748.1	1.21	1744	2.7398	2.8030	0.0632	36
03/08/2021	Sunny	7639.4	7663.4	1440.0	39	40	39.5	28.2	747.9	1.17	1681	2.7712	2.8046	0.0334	20
09/08/2021	Fine	7663.4	7687.4	1440.0	40	40	40.0	29.1	754.1	1.23	1765	2.7652	2.8058	0.0406	23
14/08/2021	Cloudy	7687.4	7711.4	1440.0	39	39	39.0	28.0	754.8	1.16	1667	2.7636	2.8025	0.0389	23
20/08/2021	Fine	7711.8	7735.8	1440.0	39	40	39.5	29.5	757.1	1.25	1799	2.7645	2.8060	0.0415	23
26/08/2021	Sunny	7735.8	7759.8	1440.0	39	39	39.0	29.7	758.3	1.21	1748	2.8098	2.8361	0.0263	15
1/09/2021	Cloudy	7760.1	7784.1	1440.0	40	40	40.0	28.7	757.4	1.20	1734	2.7659	2.7912	0.0253	15
7/09/2021	Sunny	7784.1	7808.1	1440.0	40	40	40.0	30.1	757.8	1.20	1728	2.776	2.813	0.0370	21
13/09/2021	Sunny	7808.1	7832.1	1440.0	40	41	40.5	30.9	755.0	1.22	1755	2.7569	2.8186	0.0617	35
18/09/2021	Sunny	7832.4	7856.4	1440.0	39	39	39.0	30.2	758.3	1.17	1691	2.7628	2.7985	0.0357	21
24/09/2021	Fine	7856.4	7880.4	1440.0	40	40	40.0	29.4	760.2	1.25	1794	2.7645	2.8145	0.0500	28
29/09/2021	Fine	7880.4	7904.4	1440.0	39	40	39.5	29.7	756.2	1.20	1729	2.7754	2.8833	0.1079	62

Min: 15 Max: 62


Avg:

: 26



Calibration information for Location A10										
Date of Calibration:	5-Jul-21	Slope =	12.7251							
Calibration due date:	18-Jul-21	Intercept =	22.3945							
Date of Calibration:	16-Jul-21	Slope =	12.8745							
Calibration due date:	29-Jul-21	Intercept =	22.9191							
Date of Calibration:	03-Aug-21	Slope =	12.7641							
Calibration due date:	16-Aug-21	Intercept =	23.7675							
Date of Calibration:	20-Aug-21	Slope =	12.5464							
Calibration due date:	02-Sep-21	Intercept =	23.3805							
Date of Calibration:	01-Sep-21	Slope =	15.7329							
Calibration due date:	14-Sep-21	Intercept =	20.6692							
Date of Calibration:	18-Sep-21	Slope =	15.9347							
Calibration due date:	01-0ct-21	Intercept =	19.8619							



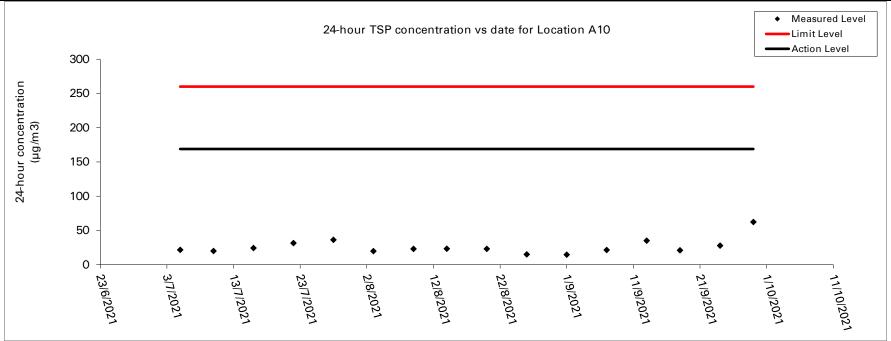



Start Date	Weather	Weather Condition Elapse Time		ıe	Chart Reading		Avg Air Temp	Avg Atmospheric Pressure	Flow Rate	Standard Air Volume		Weight g)	Particulate weight	Conc.	
	Condition	Initial	Final	Actual (min)	Min	Max	Avg	(°C)	(mm Hg)	(m³/min)	(m³)	Initial	Final	(g)	(μg/m³)
05/07/2021	Sunny	7783.4	7807.4	1440.0	39	40	39.5	30.2	755.6	1.17	1680	2.7363	2.7595	0.0232	14
10/07/2021	Sunny	7807.4	7831.4	1440.0	40	40	40.0	30.5	757.8	1.22	1755	2.7461	2.7724	0.0263	15
16/07/2021	Sunny	7831.7	7855.7	1440.0	38	39	38.5	29.6	756.4	0.98	1410	2.7416	2.7803	0.0387	27
22/07/2021	Sunny	7855.7	7879.7	1440.0	39	39	39.0	29.3	750.8	1.00	1437	2.7373	2.7879	0.0506	35
28/07/2021	Sunny	7879.7	7903.7	1440.0	39	40	39.5	30.8	748.1	1.02	1468	2.7488	2.8040	0.0552	38
03/08/2021	Sunny	7904.1	7928.1	1440.0	40	41	40.5	28.2	747.9	1.15	1657	2.7432	2.7708	0.0276	17
09/08/2021	Fine	7928.1	7952.1	1440.0	41	41	41.0	29.1	754.1	1.21	1748	2.7701	2.8033	0.0332	19
14/08/2021	Cloudy	7952.1	7976.1	1440.0	40	41	40.5	28.0	754.8	1.18	1703	2.779	2.7983	0.0193	11
20/08/2021	Fine	7976.5	8000.5	1440.0	39	39	39.0	29.5	757.1	1.12	1613	2.7750	2.8073	0.0323	20
26/08/2021	Sunny	8000.5	8024.5	1440.0	40	40	40.0	29.7	758.3	1.21	1736	2.7731	2.7908	0.0177	10
1/09/2021	Cloudy	8024.8	8048.8	1440.0	40	40	40.0	28.7	757.4	1.23	1769	2.7659	2.789	0.0231	13
7/09/2021	Sunny	8048.8	8072.8	1440.0	39	40	39.5	30.1	757.8	1.19	1713	2.7639	2.7953	0.0314	18
13/09/2021	Sunny	8072.8	8096.8	1440.0	40	40	40.0	30.9	755.0	1.21	1742	2.7689	2.8297	0.0608	35
18/09/2021	Sunny	8097.2	8121.2	1440.0	39	39	39.0	30.2	758.3	1.26	1821	2.7734	2.8074	0.0340	19
24/09/2021	Fine	8121.2	8145.2	1440.0	39	40	39.5	29.4	760.2	1.31	1888	2.7735	2.8180	0.0445	24
29/09/2021	Fine	8145.2	8169.2	1440.0	39	39	39.0	29.7	756.2	1.26	1813	2.7706	2.8650	0.0944	52

Min: 10 Max: 52


Avg:

23



Calibration information for Location A20										
Date of Calibration:	5-Jul-21	Slope =	11.3512							
Calibration due date:	18-Jul-21	Intercept =	25.6869							
Date of Calibration:	16-Jul-21	Slope =	11.9955							
Calibration due date:	29-Jul-21	Intercept =	26.2813							
Date of Calibration:	03-Aug-21	Slope =	12.0046							
Calibration due date:	16-Aug-21	Intercept =	25.8274							
Date of Calibration:	20-Aug-21	Slope =	12.0592							
Calibration due date:	02-Sep-21	Intercept =	25.0561							
Date of Calibration:	01-Sep-21	Slope =	14.3816							
Calibration due date:	14-Sep-21	Intercept =	21.9486							
Date of Calibration:	18-Sep-21	Slope =	13.7587							
Calibration due date:	01-0ct-21	Intercept =	21.1799							



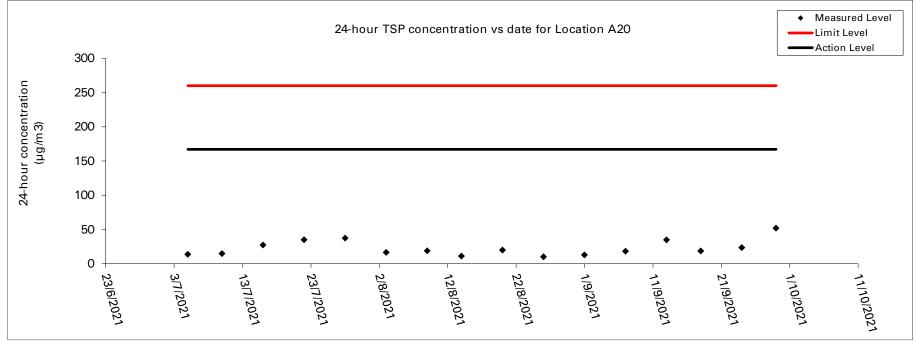





Wind direction data for 05, 10, 16, 22 and 28 July 2021

A. 05/07/2021:

Wind Direction:








B. 10/07/2021:

Wind Direction:









C. 16/07/2021:

Wind Direction:









D. 22/07/2021:

Wind Direction:









E. 28/07/2021

Wind Direction:









Wind speed data for 05, 10, 16, 22 and 28 July 2021

A. 05/07/2021:

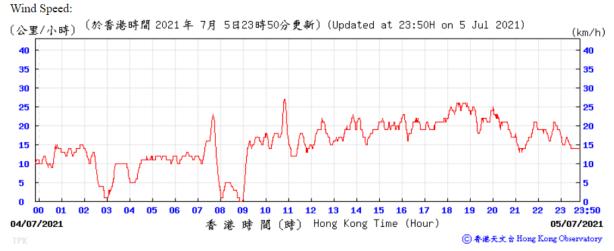







B. 10/07/2021:

Wind Speed:








C. 16/07/2021:

Wind Speed:









D. 22/07/2021:










E. 28/07/2021











Wind direction data for 03, 09, 14, 20 and 26 August 2021

A. 03/08/2021:

Wind Direction:







na Dnec	tion:
	(於香港時間 2021 年08月09日23時50分更新)(Updated at 23:50H on 9 Aug 2021)
	"風向"- 現正維修
	"Wind Direction" - Under Maintenance.
	© 春港天文台 Hong Kong Obse
nd Direc	tion:
	(於香港時間 2021 年08月10日23時50分更新)(Updated at 23:50H on 10 Aug 2021)
	"風向"- 現正維修
	"Wind Direction" - Under Maintenance.

⑥ 香港天文台 Hong Kong Observatory




· ma Dn	rection:
	(於香港時間 2021 年08月14日23時50分更新)(Updated at 23:50H on 14 Aug 2021)
	"風向"- 現正維修
	"Wind Direction" - Under Maintenance.
	Azid bir oction — oldor lidzīvolidioc.
	⑥ 香港天文台 Hong Kong Observa
ind Dir	rection:
	(於香港時間 2021 年08月15日23時50分更新)(Updated at 23:50H on 15 Aug 2021)
	"風向"- 現正維修
	"Mind Direction" - Under Maintenance.

© 香港天文 à Hong Kong Observatory



D. 20/08/2021:

Wind Direction:









E. 26/08/2021

Wind Direction:








Wind speed data for 03, 09, 14, 20 and 26 August 2021

A. 03/08/2021:

Wind Speed:







Wind Speed:	
(公里/小時)	(於香港時間 2021 年 8月 9日23時50分更新)(Updated at 23:50H on 9 Aug 2021) (km/h
	"風速"- 現正維修
	"Hind Speed" - Under Haintenance。
	⑥ 春港天文台 Hong Kong Observatory
Wind Coard.	
Wind Speed: (公里/小時)	(於香港時間 2021 年 8月10日23時50分更新)(Updated at 23:50H on 10 Aug 2021)
(公里/小时)	(km/h)
	"風速"- 現正維修
	"Mind Speed" - Under Maintenance.

⑥ 香港天文台 Hong Kong Observatory




Wind Speed:						
(公里/小時)	〔於香港時間 2021 年	8月14日23時50分更新)	(Updated at	23:50H on	14 Aug 202	1) (km/h)
		ret - k - et	+ 64.16			
		"風速"- 現』 "Hind Speed" - Under				
			•			
					◎ 香港天文会 H	ong Kong Observatory
Wind Speed:	/ 14 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	000000000000000000000000000000000000000			45 0 000	•)
〔公里/小時〕	(於香港時間 2021 年 ————————————————————————————————————	8月15日23時50分更新)	(Updated at	23:50H on	15 Aug 202	1) (km/h)
		"風速"- 現.	正錐條			
		"Wind Speed" - Under				
					◎ 香港天文会 B	long Kong Observatory



D. 20/08/2021:









E. 26/08/2021










Wind direction data for 01, 07, 13, 18, 24 and 29 September 2021

A. 01/09/2021:








B. 07/09/2021:







C. 13/09/2021:







D. 18/09/2021:








E. 24/09/2021








F. 29/09/2021









Wind speed data for 01, 07, 13, 18, 24 and 29 September 2021

A. 01/09/2021:

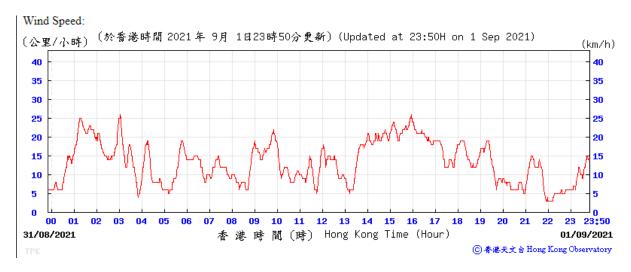


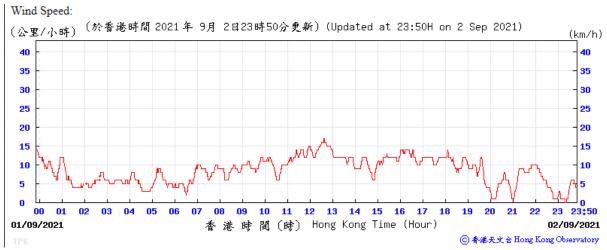



B. 07/09/2021:




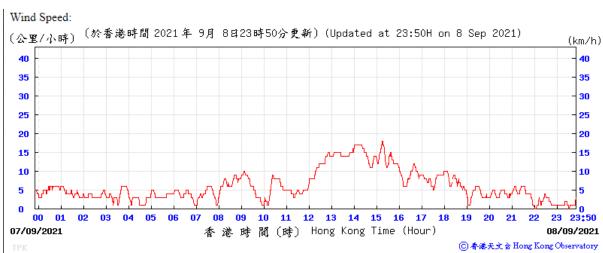




C. 13/09/2021:




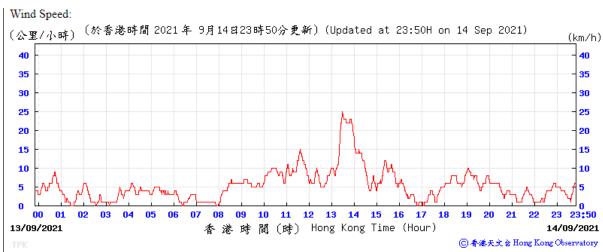



D. 18/09/2021:

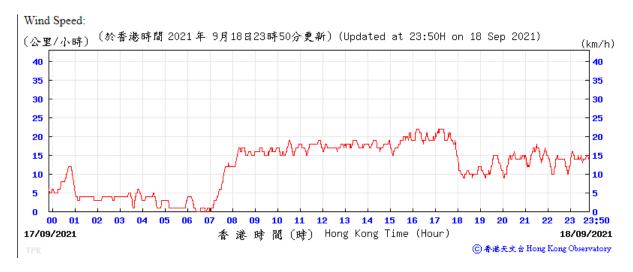

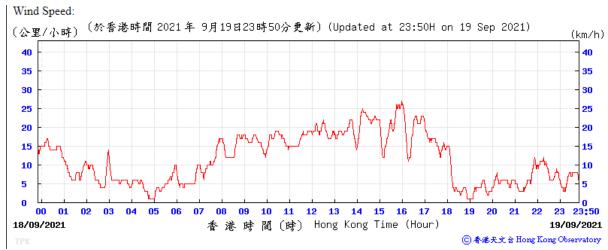




E. 24/09/2021








F. 29/09/2021

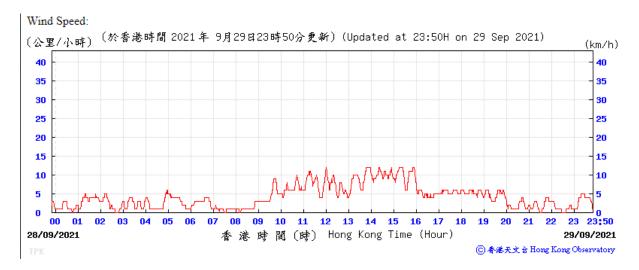

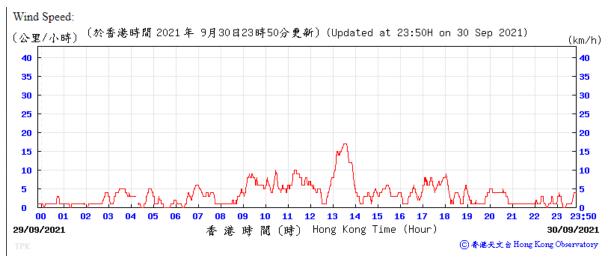



APPENDIX H: WASTE FLOW TABLE



	Actu	al Quantities	of Inert C&D	Materials Ge	enerated Month	ıly	Actual Quantities of C&D Wastes Generated Monthly					
Reporting Month	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper / cardboard packaging	Plastics (see Note)	Chemical Waste	Others, e.g. general refuse	
	(in ,000kg)	(in,000kg)	(in,000kg)	(in ,000kg)	(in ,000kg)	(in,000kg)	(in,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	(in ,000kg)	
July 2021	19.70	0	0	0	7.73	0	0	0	0	0	11.97	
August 2021	20.29	0	0	0	14.95	0	0	0	0	0	5.34	
September 2021	219.20	0	0	0	214.71	0	0	0	0	0	4.49	



Waste to Public Fill (July 2021):

Facility	Date of transactio n	Vehicle No.	Account No.	Chit No.	Time-in	Time-out	Waste depth (meter)	Weight- in (tonne)	out	weight
TM38FB	13/07/21	UW8*1	7032841	22174867	16:48	16:57	0	23.84	16.11	7.73
								Grand	Total.	7.73

Waste to Landfill (July 2021):

Facility	Date of transactio n	Vehicle No.	Account No.	Chit No.	Time-in	Time-out	Waste depth (meter)	Weight- in (tonne)	out	weight
NENT	02/07/21	LA5*81	7032841	22174865	09:52	10:20	1.03	17.86	15.77	2.09
NENT	13/07/21	LA5*81	7032841	22174866	12:31	12:52	1.03	18.24	15.79	2.45
NENT	22/07/21	LA5*81	7032841	22174868	10:46	11:12	1.18	18.53	15.72	2.81
NENT	23/07/21	LA5*81	7032841	22174869	11:16	11:50	1.23	17.91	15.8	2.11
NENT	28/07/21	LA5*81	7032841	22174870	15:00	15:24	1.12	18.34	15.83	2.51
								Grand	Total:	11.97

Waste to Public Fill (August 2021):

Facility	Date of transactio n	Vehicle No.	Account No.	Chit No.	Time-in	Time-out	Waste depth (meter)	Weight- in (tonne)	Weight- out (tonne)	Net weight (tonne)
TM38FB	31/08/21	UK6*23	7032841	22174873	09:37	09:47	0	28.71	14.28	14.43
TM38FB	31/08/21	UK6*23	7032841	22174874	11:46	11:58	0	29.2	14.25	14.95
								Grand	Total:	14.95

Waste to Landfill (August 2021):

Facility	Date of transactio n	Vehicle No.	Account No.	Chit No.	Time-in	Time-out	Waste depth (meter)	Weight- in (tonne)	Weight- out (tonne)	Net weight (tonne)
NENT	05/08/21	LA5*81	7032841	22174871	10:31	10:58	1.16	19.02	15.89	3.13
NENT	21/08/21	LA5*81	7032841	22174872	09:52	10:18	1.31	17.9	15.69	2.21
								Grand	Total:	5.34

Waste to Public Fill (August 2021):

Facility	Date of transactio n	Vehicle No.	Account No.	Chit No.	Time-in	Time-out	Waste depth (meter)	Weight- in (tonne)	Weight- out (tonne)	Net weight (tonne)
TM38FB	02/09/21	UK6*23	7032841	22174875	17:00	17:08	0	29.15	14.19	14.96
TM38FB	03/09/21	UK6*23	7032841	22174876	14:25	14:34	0	29.24	14.21	15.03
TM38FB	03/09/21	UK6*23	7032841	22174877	16:20	16:28	0	29.09	14.19	14.9
TM38FB	06/09/21	TD7*00	7032841	22174878	09:24	09:31	0	29.94	13.71	16.23
TM38FB	06/09/21	UK6*23	7032841	22174879	17:03	17:12	0	29.27	14.23	15.04
TM38FB	09/09/21	UK6*23	7032841	22174881	16:54	17:06	0	29.82	14.29	15.53
TM38FB	11/09/21	UN8*13	7032841	22174882	09:46	09:54	0	29.38	13.96	15.42
TM38FB	15/09/21	FM1*5	7032841	22174883	10:15	10:29	0	29.39	13.87	15.52
TM38FB	15/09/21	FM1*5	7032841	22174884	12:26	12:33	0	29.22	13.84	15.38
TM38FB	16/09/21	FM1*5	7032841	22174885	15:50	15:57	0	29.54	13.86	15.68
TM38FB	16/09/21	UK6*23	7032841	22174886	17:05	17:14	0	28.90	14.14	14.76
TM38FB	17/09/21	FM1*5	7032841	22174887	15:36	15:44	0	29.32	13.85	15.47
TM38FB	29/09/21	UK6*23	7032841	22174889	09:22	09:29	0	29.49	14.15	15.34
TM38FB	30/09/21	UK6*23	7032841	22174890	09:22	09:30	0	29.66	14.21	15.45
								Grand	Total:	214.71


Waste to Landfill (August 2021):

Facility	Date of transactio n	Vehicle No.	Account No.	Chit No.	Time-in	Time-out	Waste depth (meter)	Weight- in (tonne)	Weight- out (tonne)	Net weight (tonne)
NENT	08/09/21	LA5*81	7032841	22174880	10:27	10:52	1.05	18.11	15.89	2.22
NENT	18/09/21	LA5*81	7032841	22174888	09:56	10:19	1.10	18.29	16.02	2.27
								Grand	Total:	4.40




APPENDIX I: TRANSPORTATION ROUTES TO/FROM THE SITE



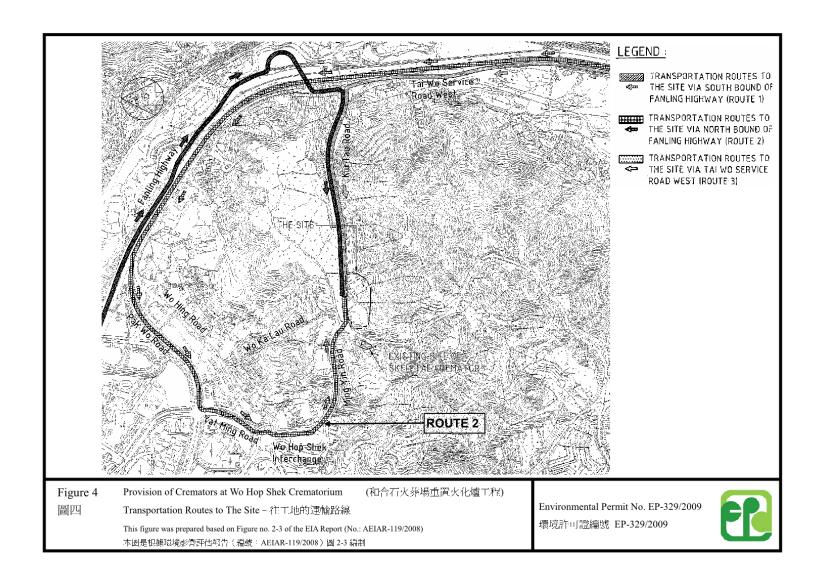



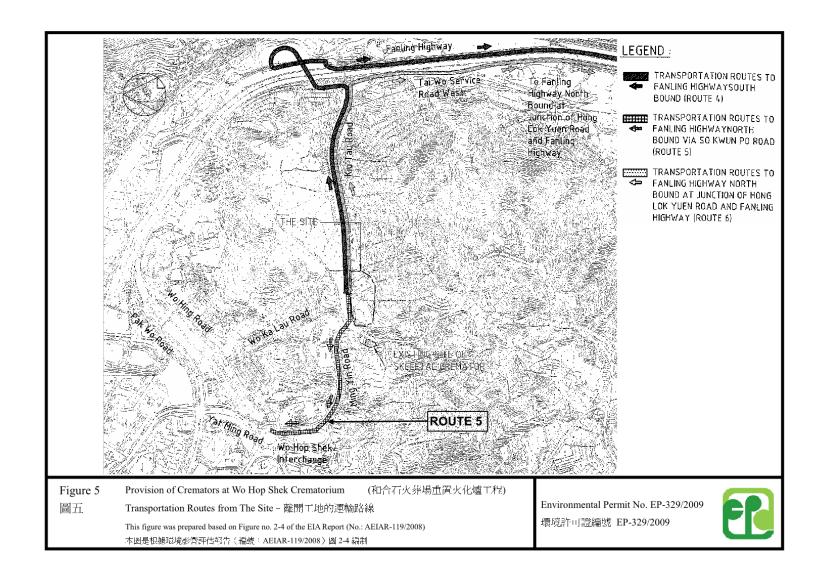



APPENDIX J: STATISTICS ON COMPLAINT, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS



Statistical Summary of Exceedances

	Air Quality								
Location	Location Action Level Limit Level Total								
A10	A10 0 0								
A20	A20 0 0								

Statistical Summary of Environmental Complaints

Reporting	Envir	onmental Complaint Sta	tistics
Period	Frequency	Cumulative	Complaint Nature
1 Jul 2021 – 30 Sep 2021	0	0	N/A

Statistical Summary of Environmental Non-compliance

Reporting	Environi	mental Non-compliance	Statistics
Period	Frequency	Cumulative	Details
1 Jul 2021 – 30 Sep 2021	0	0	N/A

Statistical Summary of Environmental Summons

Reporting	Envir	onmental Summons Sta	tistics
Period	Frequency	Cumulative	Details
1 Jul 2021 – 30 Sep 2021	0	0	N/A

Statistical Summary of Environmental Prosecution

Reporting Period	Enviro	nmental Prosecution Sta	atistics
Period	Frequency	Cumulative	Details
1 Jul 2021 – 30 Sep 2021	0	0	N/A
