


JOB No.: TCS/00280/05**REVISION No.: 1****DRAINAGE SERVICES DEPARTMENT (DSD)
CONTRACT NO. DC/2004/08****PENG CHAU SEWAGE TREATMENT WORKS
UPGRADE****MONTHLY ENVIRONMENTAL MONITORING AND
AUDIT (EM&A) REPORT FOR AUGUST 2008****PREPARED FOR****ACCIONA-ATAL JOINT VENTURE (AAJV)****Quality Index**

Date	Reference No.	Prepared By	Certified By
04 September 2008	TCS00280/05/600/R0376	Ben Tam	Ken Wong



Environmental Consultant	Environmental Team Leader
--------------------------	---------------------------

Rev. No.	Date	Remarks
1	04 September 2008	First Submission

This report has been prepared by Action-United Environmental Services & Consulting with all reasonable skill, care and diligence within the terms of the Agreement with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies upon the report at their own risk.

TABLE OF CONTENTS

1.0 INTRODUCTION	1
2.0 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	2
3.0 SUMMARY OF IMPACT MONITORING REQUIREMENTS	3
4.0 IMPACT MONITORING METHDOLOGY	5
5.0 IMPACT MONITORING RESULTS	9
6.0 WASTE MANAGEMENT	10
7.0 SITE INSPECTION	11
8.0 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	12
9.0 IMPLEMENTATION STATUS OF MITIGATION MEASURES	13
10.0 IMPACT FORECAST	14
11.0 CONCLUSION	15

LIST OF TABLES

TABLE 2-1	MAJOR CONSTRUCTION ACTIVITIES IN THE REPORTING MONTH
TABLE 2-2	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	ACTION AND LIMIT LEVELS FOR AIR QUALITY
TABLE 3-3	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 3-4	ACTION AND LIMIT LEVELS FOR MARINE WATER QUALITY
TABLE 4-1	LOCATION OF AIR QUALITY AND NOISE MONITORING STATION
TABLE 4-2	LOCATIONS OF MARINE WATER QUALITY MONITORING
TABLE 4-3	MONITORING EQUIPMENT USED IN EM&A PROGRAM
TABLE 4-4	ANALYTICAL METHODS APPLIED TO MARINE WATER QUALITY SAMPLES
TABLE 5-1	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS
TABLE 5-2	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS
TABLE 6-1	SUMMARY OF WASTE QUANTITIES FOR DISPOSAL
TABLE 6-2	SUMMARY OF QUANTITIES OF RECYCLING MATERIALS
TABLE 8-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 11-1	SUMMARY OF THE EXCEEDANCES FOR IMPACT MONITORING

LIST OF APPENDICES

APPENDIX A	PROJECT SITE LAYOUT
APPENDIX B	ENVIRONMENTAL ORGANISATION STRUCTURE
APPENDIX C	LOCATIONS OF DESIGNATED MONITORING STATIONS
APPENDIX D	EQUIPMENT CALIBRATION CERTIFICATES
APPENDIX E	IMPACT MONITORING SCHEDULES
APPENDIX F	GRAPHICAL PLOTS OF AIR QUALITY AND CONSTRUCTION NOISE MONITORING RESULTS
APPENDIX G	METEOROLOGICAL DATA IN THE REPORTING PERIOD
APPENDIX H	THREE-MONTH ROLLING PROGRAM

EXECUTIVE SUMMARY

- ES01. Acciona-ATAL Joint Venture (AAJV) has been awarded the DSD Contract DC/2004/08 (Project) for the Peng Chau Sewage Treatment Works Upgrade in May 2005. The Project requires an Environmental Monitoring & Audit (EM&A) program to be implemented by an Environmental Team (ET) throughout the contract period in compliance with the requirements as stated in the project Environmental Permit (EP-203/2004) and the Project EM&A Manual.
- ES02. Action-United Environmental Services and Consulting (AUES) had been commissioned by AAJV to be an independent Environmental Team (ET) to implement the EM&A program in compliance with the EP and the project EM&A Manual.
- ES03. This report presents the monitoring results and audit findings under the EM&A program during the reporting month for **August 2008**.

EM&A ACTIVITIES IN THE REPORTING MONTH

- ES04. A summary of the monitoring activities in this reporting month is listed below:

• 1-Hour TSP Monitoring	15 Events
• 24-Hour TSP Monitoring	5 Events
• Construction Noise Monitoring	5 Events
• Marine Water Quality Monitoring	0 Event
• Site Inspection Audit	5 Times

AIR QUALITY

- ES05. No exceedances of 1-Hour and 24-Hour TSP measurements were recorded in this reporting month.

CONSTRUCTION NOISE

- ES06. No Limit Level exceedance in construction noise measurements was recorded and no noise complaint (Action Level) was received in this reporting month.

MARINE WATER QUALITY

- ES07. The marine based construction activities had been completed on 1 August 2006, post marine water quality monitoring was commenced on 2 August 2006 and completed on 1 September 2006 in accordance with Clause 4.32 of the EM&A Manual. All the measurement results at the control/impact stations were within the baseline range. The monitoring results were presented in the previous Monthly EM&A Report (September 2006).

SUMMARY OF MONITORING EXCEEDANCES

ES08. A summary of monitoring exceedances in this reporting month for air quality, construction noise and marine water quality monitoring are presented below:-

Env. Quality	Parameters	Compliance %	Investigation & Corrective Actions
Air Quality	1-Hour TSP	100	Not Required for 100% Compliance
	24-Hour TSP	100	Not Required for 100% Compliance
Noise	Leq (30min) Daytime	100	Not Required for 100% Compliance
Marine Water Quality*	-	-	-

Note: * No marine water quality impact monitoring was required since all marine based construction activities were completed on 01 August 2006.

ENVIRONMENTAL COMPLAINTS

ES09. No environmental complaint was received in this reporting month.

ENVIRONMENTAL SUMMONS

ES10. No environmental summons was received in this reporting month.

FUTURE KEY ISSUES

ES11. In according to the Contractor information via e-mail, the major construction activity of the captioned project will be completed at the end of **August 2008**. Therefore, the EM&A program will terminate at end of August 2008 and no environmental monitoring will be conducted after 31 August 2008. Since no major construction activity will undertake after 31 August 2008, no environmental issues to be considered in the coming month.

1.0 INTRODUCTION

- 1.01 Acciona-ATAL Joint Venture (AAJV) has been awarded the DSD Contract DC/2004/08 (Project) for the upgrading of Peng Chau Sewage Treatment Works in May 2005. The Project requires an Environmental Monitoring & Audit (EM&A) program to be implemented by an Environmental Team (ET) throughout the contract period in compliance with the requirements as stated in the project Environmental Permit (EP-203/2004) and the project EM&A manual. The location of the project site is presented in **Appendix A**.
- 1.02 The works to be executed under this project mainly comprise the following:-
- Upgrade and reconstruct the existing Peng Chau Sewage Treatment Works (STW);
 - Construct an emergency overflow, storm tanks and submarine outfall;
 - Provide de-odourization facilities and associated sludge treatment facilities, and extend inlet pumping mains and construct an equalization tank;
 - Demolish the existing treatment facilities;
 - Construct sludge drying bed; and
 - Construct remaining works
- 1.03 Action-United Environmental Services and Consulting (AUES) had been commissioned by AAJV to be the independent environmental team (ET) for implementation of the EM&A program in accordance with the requirements as set out in the EP and the project EM&A manual.
- 1.04 This report presents the monitoring results and audit findings under the EM&A program during the reporting month for **August 2008**.

REPORT STRUCTURE

- 1.05 The Monthly EM&A report is structured into the following sections:-

SECTION 1	INTRODUCTION
SECTION 2	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS
SECTION 3	SUMMARY OF IMPACT MONITORING REQUIREMENTS
SECTION 4	IMPACT MONITORING METHODOLOGIES
SECTION 5	IMPACT MONITORING RESULTS
SECTION 6	WASTE MANAGEMENT
SECTION 7	SITE INSPECTION
SECTION 8	ENVIRONMENTAL COMPLAINTS AND NON-COMPLIANCE
SECTION 9	IMPLEMENTATION STATUSES OF MITIGATION MEASURES
SECTION 10	IMPACT FORECAST
SECTION 11	CONCLUSIONS

2.0 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS**PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE**

- 2.01 The organization chart and lines of communication with respect to the on-site environmental management and monitoring program are shown in **Appendix B**.

CONSTRUCTION PROGRESS

- 2.02 A summary of the major construction activities undertaken in this reporting month is shown in **Table 2-1**.

Table 2-1 Major Construction Activities in the Reporting Month

Locations	Description of Construction Activities
Portion P	—
Portion Q	—
Portion R	<ul style="list-style-type: none"> • Glazing works of Drying Bed House; • Paving works construction; and • Painting works at NSTC and DBH
Portion S	—
Area A	—
Area B	—
Area C	<ul style="list-style-type: none"> • Removing existing concrete slab

SUMMARY OF ENVIRONMENTAL SUBMISSIONS

- 2.03 A summary of the relevant permits, licences, and/or notifications on environmental protection for the Project during this reporting month is presented in **Table 2-2**.

Table 2-2 Status of Environmental Licenses and Permits

Items	Item Description	License/Permit Status
1	Environmental Permit No. : EP-203/2004	Issued at 30 November 2004
2	Air Pollution Control (Construction Dust)	Notified EPD on 17 June 2005
3	Water Pollution Control (Discharge Licence) No.: EP890/W2/XE005	Valid to 30 September 2010
4	Chemical Waste Producer Registration No.: WPN:5213-976-N2449-01	Registration on 03 June 2005
5	Exemption for site concrete batching plant licence	Issued at 21 October 2005
6	Exemption Account for Disposal of Construction Waste (Account Number : 5000577)	Valid until 27 September 2008

3.0 SUMMARY OF IMPACT MONITORING REQUIREMENTS

- 3.01 Environmental monitoring and audit requirements are set out in the project EM&A manual. Air quality, construction noise and marine water quality have been identified as the key environmental issues under this project during the construction phase.
- 3.02 A summary of the EM&A requirements for air quality, construction noise and marine water quality monitoring are shown in **Table 3-1**. The designated station/locations for air quality, construction noise and marine water quality monitoring are shown in **Appendix C**.

Table 3-1 Summary of EM&A Requirements

Environmental Aspect	Monitoring Parameters	
Air Quality	1-Hour TSP	
	24-Hour TSP	
Construction Noise	Leq _(30min) during normal working hours	
	Supplementary L ₁₀ and L ₉₀ for reference.	
Marine Water Quality	<ul style="list-style-type: none"> • Dissolved Oxygen (DO); • Temperature; • Turbidity; • pH; 	<ul style="list-style-type: none"> • Salinity; • Suspended Solids (SS); • Ammonia Nitrogen; and • Total Inorganic Nitrogen.

- 3.03 Air quality monitoring is carried out once in every six days for 24-Hour TSP and 3 times every six days for 1-Hour TSP at the designated monitoring station.
- 3.04 Construction noise monitoring is conducted once in every six days at the designated monitoring station. Measurements of Leq_(30min) shall be taken between 0700 and 1900 with supplementary L₁₀ and L₉₀ data will be collected.
- 3.05 Marine water quality monitoring is carried out 3 times every week at 4 designated monitoring locations (2 Control stations and 2 Impact stations).
- 3.06 The impact marine water quality monitoring program shall be conducted during the course of marine based construction activities of the Project.
- 3.07 A summary of the Action/Limit (A/L) Levels for air quality, construction noise and marine water quality are shown in **Tables 3-2, 3-3 and 3-4**.

Table 3-2 Action and Limit Levels for Air Quality

Monitoring Location	Action Level ($\mu\text{g}/\text{m}^3$)		Limit Level ($\mu\text{g}/\text{m}^3$)	
	1-Hour TSP	24-Hour TSP	1-Hour TSP	24-Hour TSP
AN1	> or = 346	> or = 163	> or = 500	> or = 260

Table 3-3 Action and Limit Levels for Construction Noise

Monitoring Period	Action Level in dB(A)	Limit Level in dB(A)
0700-1900 hours on normal weekdays	When one or more documented complaint was received	> 75 dB(A)

Table 3-4 Action and Limit Levels for Marine Water Quality

Parameters		Action Level	Limit Level
DO mg/L	Surface & Mid-depth	< or = 4.1	< or = 3.9
	Bottom	< or =3.3	< or = 2.0
Turbidity, NTU		6.2 or 120% of upstream control station's SS at the same tide of the same day.	7.5 or 130% of upstream control station's SS at the same tide of the same day.
SS, mg/L		17.6 or 120% of upstream control station's SS at the same tide of the same day.	20.2 or 130% of upstream control station's SS at the same tide of the same day.
NH3-N, mg/L		> or = 0.16	> or = 0.22
TIN, mg/L		> or = 0.91	> or = 0.94
E.Coli, cfu/100mL		> or = 374	> or = 610

3.08 The Event Action Plan for air quality, construction noise and marine water quality has been implemented in this project. Details of the Event Action Plan were presented in the First Impact EM&A report.

4.0 IMPACT MONITORING METHDOLOGY

MONITORING LOCATIONS

- 4.01 There is one designated station for air quality and construction noise monitoring and four (4) designated locations for marine water quality monitoring. Their locations are shown in **Tables 4-1** and **4-2** and geographically in **Appendix C**.
- 4.02 Owing to the residents' refusal of providing access to the designated air quality and construction noise station, an alternative air and noise monitoring station was proposed and approved by EPD (Ref: (2) EP2/N9/F/93 IV) on 14 July 2005. The approved alternative air and noise station is located at the abutment (Portion P) within the site boundary next to the sensitive receiver Sea Crest Villa.

Table 4-1 Location of Air Quality and Noise Monitoring Station

Station ID	Description
AN1	Abutment at Portion P next to Sea Crest Villa

Table 4-2 Locations of Marine Water Quality Monitoring

Locations ID	Description	Easting	Northing
W1	Predicted Dredging Non-Impact Zone	821279.0	816452.1
W2	Live Coral Area	821573.2	816769.7
C1	Control Station	821919.0	817155.0
C2	Control Station	821443.2	816257.4

- 4.03 The installation of a wind monitoring station at the sensitive receivers or site offices was confirmed impractical. Use of meteorological data provided by the Peng Chau Station of the Hong Kong Observatory (HKO) has been adopted in this project since September 2005.

MONITORING FREQUENCY AND PERIOD

1-HOUR TSP MONITORING

- 4.04 All 1-Hour TSP monitoring was conducted at the EPD-approved alternative station three times every 6 days.

24-HOUR TSP MONITORING

- 4.05 All 24-Hour TSP monitoring was conducted at the EPD-approved alternative station once every six days.

CONSTRUCTION NOISE MONITORING

- 4.06 Impact construction noise monitoring was undertaken at the EPD approved alternative location weekly.

MARINE WATER QUALITY MONITORING

- 4.07 Since the submarine work was completed on 01 August 2006, therefore no impact water quality monitoring had been undertaken in this reporting period. According to the EM&A Clause 4.32, post water quality monitoring had been conducted from 02 August 2006 to 01 September 2006. All the measurement results at the control/impact stations were within the baseline range. The monitoring results were presented in the pervious Monthly EM&A Report (September 2006).

MONITORING EQUIPMENT

- 4.08 The monitoring equipment used by the ET in the EM&A program is presented in the **Table 4-3**.

Table 4-3 Monitoring Equipment Used in EM&A Program

Environmental Aspect	Parameters	Monitoring Equipment
Marine Water Quality	Dissolved Oxygen	YSI 85
	Temperature	YSI 85
	Turbidity	HACH 2100P
Air Quality	1-Hour TSP	Sibata LD-3
	24-Hour TSP	Tisch High Volume Sampler 515N
Construction Noise	Leq30	B&K Type 2238
	Acoustical Calibrator	B&K Type 4231

1-HOUR TSP MONITORING

- 4.09 Measurement of 1-Hour TSP monitoring was taken by a Sibata LD-3 Laser Dust Meter that is a portable and battery-operated laser photometer capable of performing real time 1-Hour TSP measurements. A comparison test with HVS was carried out prior to baseline monitoring in compliance with the EM&A requirements and a conversion factor for direct reading of the dust meter has been established.

24-HOUR TSP MONITORING

- 4.10 The 24-Hour TSP monitoring was carried out by a High Volume Sampler (HVS) in compliance with the project EM&A Manual. The HVS employed complied with the PS specifications including.

- Power supply of 220v/50 Hz for 24-Hour continuous operation;
- 0.6-1.7 m³/min (20-60 SCFM) adjustable flow rate;
- A 7-day mechanical timer for 24-Hour operation;
- An elapsed time indicator with ± 2 minutes accuracy for 24-Hour operation;
- Minimum exposed area of 63 in²;
- Flow control accuracy of $\pm 2.5\%$ deviation over 24-Hour operation;
- An anodized aluminum shelter to protect the filter and sampler;
- A motor speed-voltage control to control mass flow rate with accuracy of $\pm 2.5\%$ deviation over 24-Hour sampling period;
- Provision of a flow recorder for continuous monitoring;
- Provision of a peaked roof inlet;
- Incorporation with a manometer; and
- An 8"x10" stainless steel filter holder to hold, seal and easy to change the filter paper.

- 4.11 The filter papers used in 24-Hour TSP monitoring were of size 8"x10" and provided by a local HOKLAS-accredited laboratory, ALS Techichem Pty (HK) Limited (HOKLAS No. 66). The filters papers after measurements were returned to the laboratory for the required treatment and analysis.

WIND DATA MONITORING

- 4.12 The installation of a wind monitoring station at the sensitive receivers or site offices was confirmed impractical. The meteorological data for this project has been provided by the Hong Kong Observatory (HKO) Peng Chau Station upon IEC and EPD approval.

NOISE MONITORING

- 4.13 Noise measurements were taken in terms of the A-weighted equivalent sound pressure level (Leq) measured in decibels (dB). Supplementary statistical results such as L₁₀ and L₉₀ were also obtained for reference.
- 4.14 Hand-held sound level meters and associated acoustical calibrators in compliance with the International Electrotechnical Commission (IEC) Publication 651:1979 (Type 1) and 804:1985 (Type 1) specifications were used for taking the impact noise measurements.
- 4.15 Windshield was fitted in all measurements. All noise measurements were made with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq).
- 4.16 No noise measurement was carried out in the presence of fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s.

MARINE WATER QUALITY MONITORING

- 4.17 The marine water quality monitoring was carried out in compliance with the project EM&A requirements. Monitored parameters include Dissolved Oxygen (DO), Temperature, Turbidity, Salinity, pH, Suspended Solids (SS) and Total Inorganic Nitrogen (TIN).
- 4.18 DO, temperature, turbidity, pH and salinity were measured in-situ whereas SS and TIN were determined in a HOKLAS accredited laboratory.
- 4.19 Marine water quality monitoring was conducted during mid-ebb and mid-flood at specified depths in compliance with the project EM&A Manual. Duplicate in-situ measurements were taken and duplicate samples were collected in accordance with HOKLAS requirements for QA/QC purposes.

LABORATORY MEASUREMENT/ANALYSIS

- 4.20 Laboratory analyses of SS, TIN and ammonia nitrogen were carried out by a local HOKLAS- accredited laboratory, ALS Techichem Pty (HK) Limited (HOKLAS No. 066). The specified testing services provided by ALS as shown in **Table 4-4** are accredited under the HOKLAS Scheme.

Table 4-4 Analytical Methods Applied to Marine Water Quality Samples

Determinant	Standard Method	Detection Limit
Suspended Solids (mg/L)	ALS Method EA-025	2.0 mg/L
Total Inorganic Nitrogen (mg/L)	ALS Method EK-055A	0.01 mg/L
Ammonia Nitrogen (mg/L)	ALS Method EK-055A	0.01 mg/L

EQUIPMENT CALIBRATION

- 4.21 Initial calibration of the HVS was performed upon installation and thereafter at bi-monthly intervals in accordance with the manufacturer's instruction using the NIST-certified standard calibrator. The calibration data are properly documented and the records are maintained by ET for future reference.

- 4.22 The 1-Hour TSP meter was calibrated by the supplier prior to purchase. Zero response of the equipment is checked before and after each monitoring event. A comparison test was carried out with a HVS. A conversion factor (K) of 4.0 was generated in accordance with the equipment manufacturer's instruction. The meter counts in minutes multiplied by the conversion factor will generate the equivalent dust concentration by HVS.
- 4.23 The sound level meters are calibrated using an acoustical calibrator prior to and after measurements. The meters are regularly calibrated in accordance with the manufacturer's instructions. Prior to and following each noise measurement, the accuracy of the sound level meter was checked using an acoustical calibrator generating a known sound pressure level at a known frequency. Measurements are considered valid only if the calibration levels before and after the noise measurement agree to within 1.0 dB.
- 4.24 All in-situ water monitoring instruments are checked, calibrated and certified by a HOKLAS accredited laboratory before use and subsequently re-calibrated at 3-monthly intervals. Responses of sensors and electrodes are checked with standard solutions before each use.
- 4.25 The calibration certificates of the monitoring equipment used during the impact monitoring program are attached in **Appendix D**.

DATA MANAGEMENT AND DATA QA/QC CONTROL

- 4.26 The monitoring data recorded in the equipment e.g. 1-Hour TSP meters and noise meters are downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data are input into a computerized database properly maintained by the ET. The laboratory results are input directly into the computerized database and QA/QC checked by personnel other than those who input the data.
- 4.27 For monitoring activities require laboratory analysis, the local laboratory follows the QA/QC requirements as set out under the HOKLAS scheme for all laboratory testing.

5.0 IMPACT MONITORING RESULTS

5.01 The impact EM&A program was carried out by the ET in compliance with the project EM&A Manual in this reporting period. The impact monitoring schedules are presented in **Appendix E** and the monitoring results are presented in the following sub-sections.

AIR QUALITY

5.02 The impact air quality monitoring data is summarized in **Tables 5-1**. Graphical plots of the 1-Hour and 24-Hour TSP results are shown in **Appendix F** respectively.

Table 5-1 Summary of 24-Hour and 1-Hour TSP Monitoring Results

Monitoring Date	24-Hour TSP ($\mu\text{g}/\text{m}^3$)	1-Hour TSP Monitoring Results ($\mu\text{g}/\text{m}^3$)				
		Monitoring Date	Start Time	1 st Result	2 nd Result	3 rd Result
4-Aug-08	80	4-Aug-08	09:35	166	150	146
9-Aug-08	41	9-Aug-08	13:00	63	65	59
15-Aug-08	14	15-Aug-08	09:12	39	35	34
21-Aug-08	106	21-Aug-08	13:00	54	56	59
27-Aug-08	11	27-Aug-08	13:00	22	20	21
Action Level	> or = 163	-	-	> or = 346		
Limit Level	> or = 260	-	-	> or = 500		

Note: * Exceedances are in bold and underline.

5.03 No Action/Limit Level exceedance of 1-Hour and 24-Hour TSP measurements were recorded in this reporting month.

5.04 The meteorological data in this reporting month are summarized in **Appendix G**.

CONSTRUCTION NOISE

5.05 The impact noise monitoring results are summarized in **Table 5-2**. Graphical plots of the monitoring data are presented in **Appendix F**.

Table 5-2 Summary of Construction Noise Monitoring Results

Date	Start Time	1st Leq5	2nd Leq5	3rd Leq5	4th Leq5	5th Leq5	6 th Leq5	Leq30	Corrected* Leq30
4-Aug-08	09:50	59.9	53.1	56.5	51.8	58.8	54.4	56.7	59.7
9-Aug-08	13:33	60.3	58.7	62.4	61.7	59.9	57.1	60.4	63.4
15-Aug-08	09:50	65.6	67.4	60.9	60.7	67.0	62.6	64.9	67.9
21-Aug-08	13:00	55.7	58.2	49.3	54.0	56.7	53.1	55.3	58.3
27-Aug-08	13:20	65.0	54.3	66.0	63.0	65.3	67.6	64.9	67.9
Limit Level		-						-	> 75 dB(A)

Note: * A façade correction of +3 dB(A) has been added according to acoustical principles and EPD guidelines.

MARINE WATER QUALITY

5.06 No marine water quality impact monitoring was required in this reporting month since all marine based construction works had been completed on 01 August 2006.

5.07 Based on the Project EM&A Manual Clause 4.32, the post marine water quality monitoring had been conducted from 02 August 2006 to 01 September 2006. All the measurement results at the control/impact stations were within the baseline range and presented in the pervious Monthly EM&A Report (September 2006).

6.0 WASTE MANAGEMENT

6.01 The waste management inspection carried by ET was performed on 29 August 2008 in this reporting month, no observation was recorded.

RECORDS OF WASTE QUANTITIES

6.02 All types of waste arising from the construction work are classified into the following:-

- Excavated material;
- Construction & demolition (C&D) material;
- Chemical waste; and
- General refuse

6.03 The quantities of waste for disposal in this reporting month are summarized in **Tables 6-1** and **6-2**. Whenever possible, materials were reused on-site as far as practicable.

Table 6-1 Summary of Waste Quantities for Disposal

Type of Waste	Quantity	Disposal Locations
Excavated Material (Spent lube oil) (Liters)	-	N/A
Empty Site Vehicle Batteries (Nos.)	-	N/A
Excavated material (Uncontaminated) (m ³)	18.85	Peng Chau Transfer Facility
Broken Rock (m ³)	-	Peng Chau Transfer Facility
Construction & Demolition Material (Inert) (tons)	141.13	Peng Chau Transfer Facility
Construction & Demolition Material (Non-Inert) (tons)	-	N/A
Asbestos C&D Materials (m ³)	-	N/A
Chemical Waste (Liters)	-	N/A
Wastewater Collected for Off-site Treatment (m ³)	-	N/A
General Refuse (tons)	-	Peng Chau Transfer Facility
Dredged Materials (m ³)	-	N/A

Table 6-2 Summary of Quantities of Recycling Materials

Type of Waste	Quantity	Disposal Locations
Recycled Metal (kg)	-	NA
Recycled Paper (kg)	-	NA
Recycled Plastic (kg)	-	NA

7.0 SITE INSPECTION

7.01 Representatives of the Engineer and the Contractor carried out joint site inspection every week to evaluate the site environmental performance. The monthly joint IEC site audit was carried out on 29 August 2008. No non-compliance was noted and some observations were made on general site housekeeping and equipments maintenance.

7.02 Details of the observations and recommendations were recorded during the joint site inspection as follows:

- The Contractor was reminded to cover the stocks of dusty materials not being used by impervious sheeting;
- The Contractor was reminded to dispose of the C&D wastes properly, especially for chemical waste which should be collected by licensed chemical waste collector.

8.0 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE**ENVIRONMENTAL COMPLAINT AND PROSECUTION**

8.01 No environmental complaint was received in this reporting month. The statistical summary table of environmental complaint is presented in **Table 8-1**.

8.02 No environmental summons and prosecution was received in this reporting month.

Table 8-1 Statistical Summary of Environmental Complaints

Reporting Month	Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
August – December 2005	0	0	NA
January – December 2006	0	0	NA
January – December 2007	0	0	NA
January – July 2008	0	0	NA
August 2008	0	0	NA

9.0 IMPLEMENTATION STATUS OF MITIGATION MEASURES

9.01 AAJV has been implementing the required environmental mitigation measures according to the project Mitigation Implementation Schedule. The implementation schedule with mitigation measures is presented in the First Impact EM&A report.

9.02 A summary of environmental mitigation measures generally implemented by AAJV in this reporting month is presented as follows:

Water Quality

- Wastewater were appropriately treated by treatment facilities;
- Drainage channels were provided to convey run-off into the treatment facilities;
- Drainage systems were regularly and adequately maintained.

Landscaping

- Tree protection measures were provided to existing trees;
- No tree was unnecessarily lopped or felled.

Air Quality

- Vehicles were cleaned of mud and debris before leaving the site;
- Site vehicles were limited to within 15 km/hr;
- Public roads around the site entrance/exit had been kept clean and free from dust;
- Dust suppression measures were properly implemented to reduce dust emission from stockpile.

Construction Noise

- Works and equipment were located to minimize noise nuisance from the nearest sensitive receiver;
- Idle equipments were either turned off or throttled down;
- Some of the Powered Mechanical Equipments were covered or shielded by appropriate acoustic materials if practicable.

Waste and Chemical Management

- Wastes were properly segregated into inert and non-inert in appropriate containers/areas;
- Excavated materials were reused where practicable.
- A chemical waste storage area had been provided on site;

General

- The site was generally kept tidy and clean.

10.0 IMPACT FORECAST

KEY ISSUES FOR THE COMING MONTH

10.01 In according to the Contractor information via e-mail, the major construction activity of the captioned project will be completed at the end of **August 2008**. Therefore, the EM&A program will terminate at end of August 2008 and no environmental monitoring will be conducted after 31 August 2008. Since no major construction activity will undertake after 31 August 2008, no environmental issues to be considered in the coming month.

10.02 The tentative 3-month rolling program is presented in **Appendix H**.

11.0 CONCLUSION

11.01 The EM&A program in **August 2008** was undertaken in compliance with the EM&A manual for the Peng Chau Sewage Treatment Works Upgrade. A summary of environmental compliance of air quality, construction noise and marine water quality in this reporting month are presented in **Table 11-1**.

Table 11-1 Summary of the Exceedances for Impact Monitoring

Env. Quality	Parameters	Compliance %	Investigation & Corrective Actions
Air Quality	1-Hour TSP	100	Not Required for 100% Compliance
	24-Hour TSP	100	Not Required for 100% Compliance
Noise	Leq (30min) Daytime	100	Not Required for 100% Compliance
Marine Water Quality*	-	-	-

Note: * No marine water quality impact monitoring was required since all marine based construction activities were completed on 01 August 2006.

11.02 No Action/Limit Level exceedance of 1-Hour and 24-Hour TSP measurements were recorded in this reporting month.

11.03 All noise levels measured at AN1 were below the Limit level and no complaint (Action Level) was received in this reporting month.

11.04 No marine water quality impact monitoring was required in this reporting month during the course of marine works was completed on 01 August 2006.

11.05 Based on the EM&A Manual Clause 4.32, the post marine water quality monitoring was carried out from 02 August 2006 to 01 September 2006. All the monitoring results in the control/impact stations were within the baseline range. The monitoring results and graphical plot were present in pervious Monthly EM&A Report (September 2006).

11.06 No environmental complaint or summons was received in this reporting month.

RECOMMENDATIONS


11.07 Based on the IEC site inspection records on 29 August 2008 the following key recommendations are pertinent:


- The Contractor was reminded to cover the stocks of dusty materials not being used by impervious sheeting;
- The Contractor was reminded to dispose of the C&D wastes properly, especially for chemical waste which should be collected by licensed chemical waste collector.

11.08 In according to the Contractor information via e-mail, the major construction activity of the captioned project will be completed at the end of **August 2008**. Therefore, the EM&A program will terminate at end of August 2008 and no major construction activity will undertake after 31 August 2008, no environmental issues to be considered in the coming month.

APPENDIX A

PROJECT SITE LAYOUT

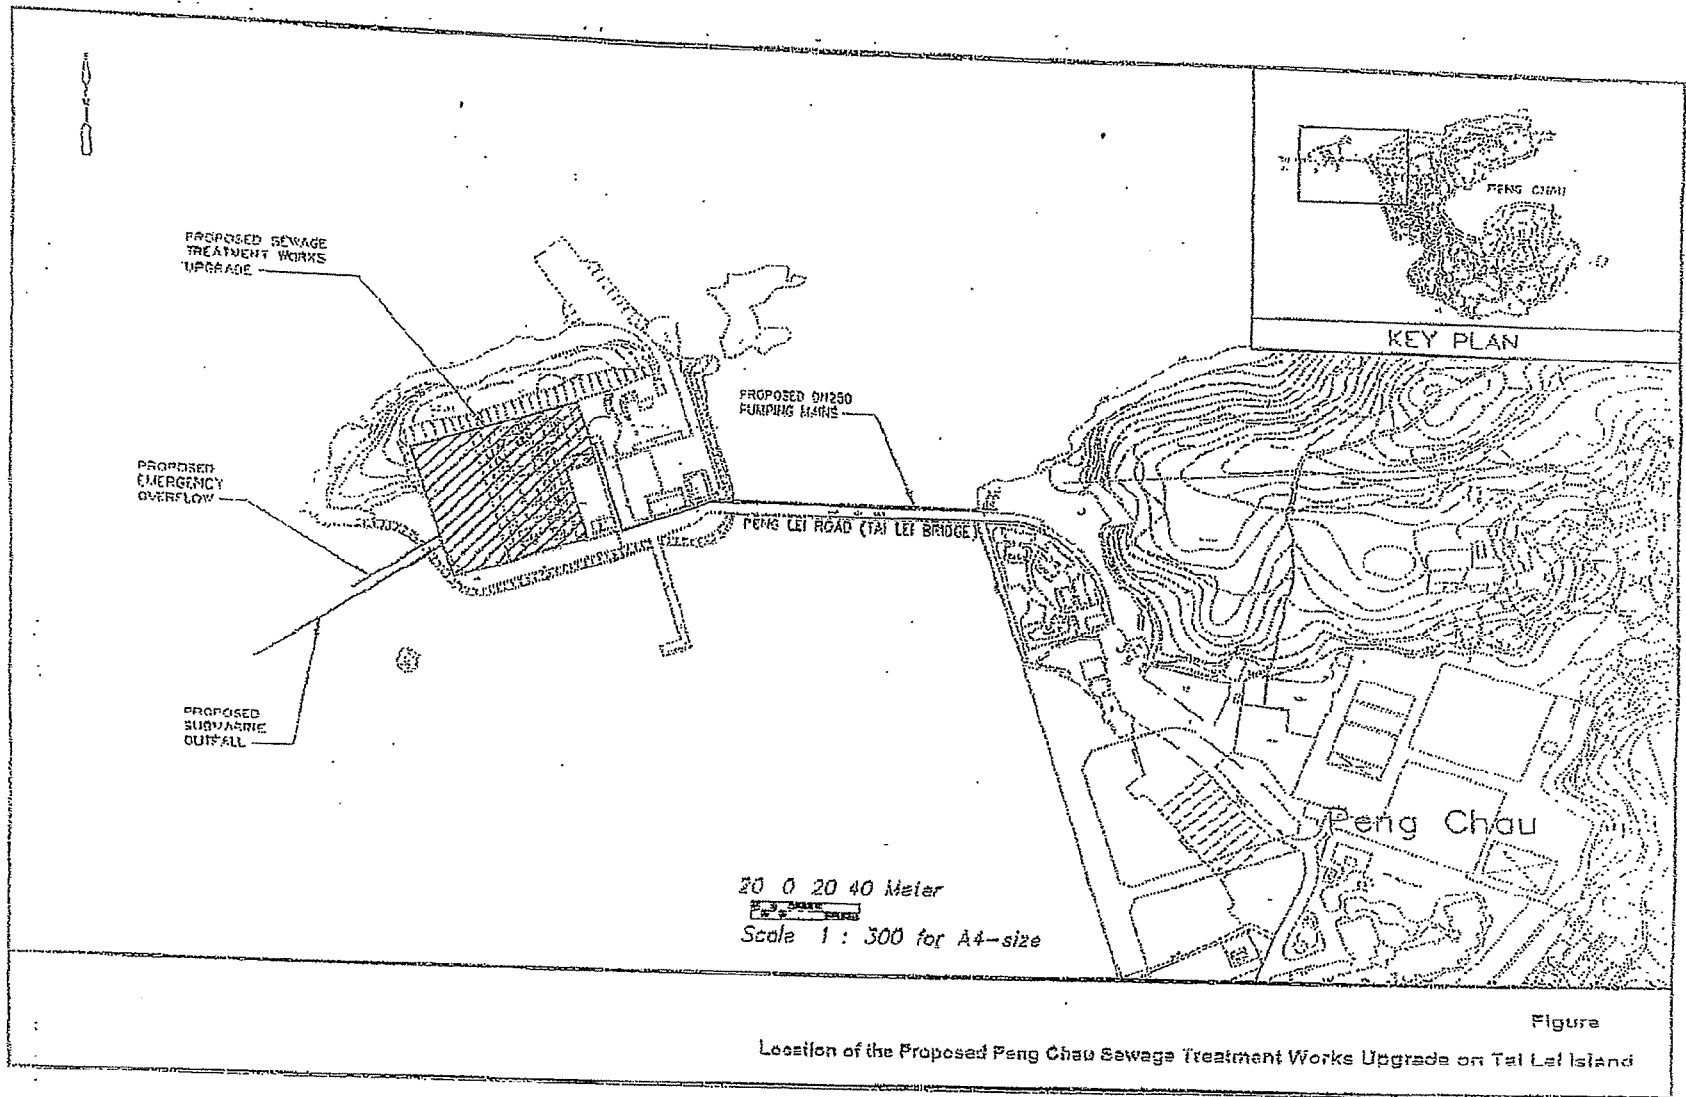

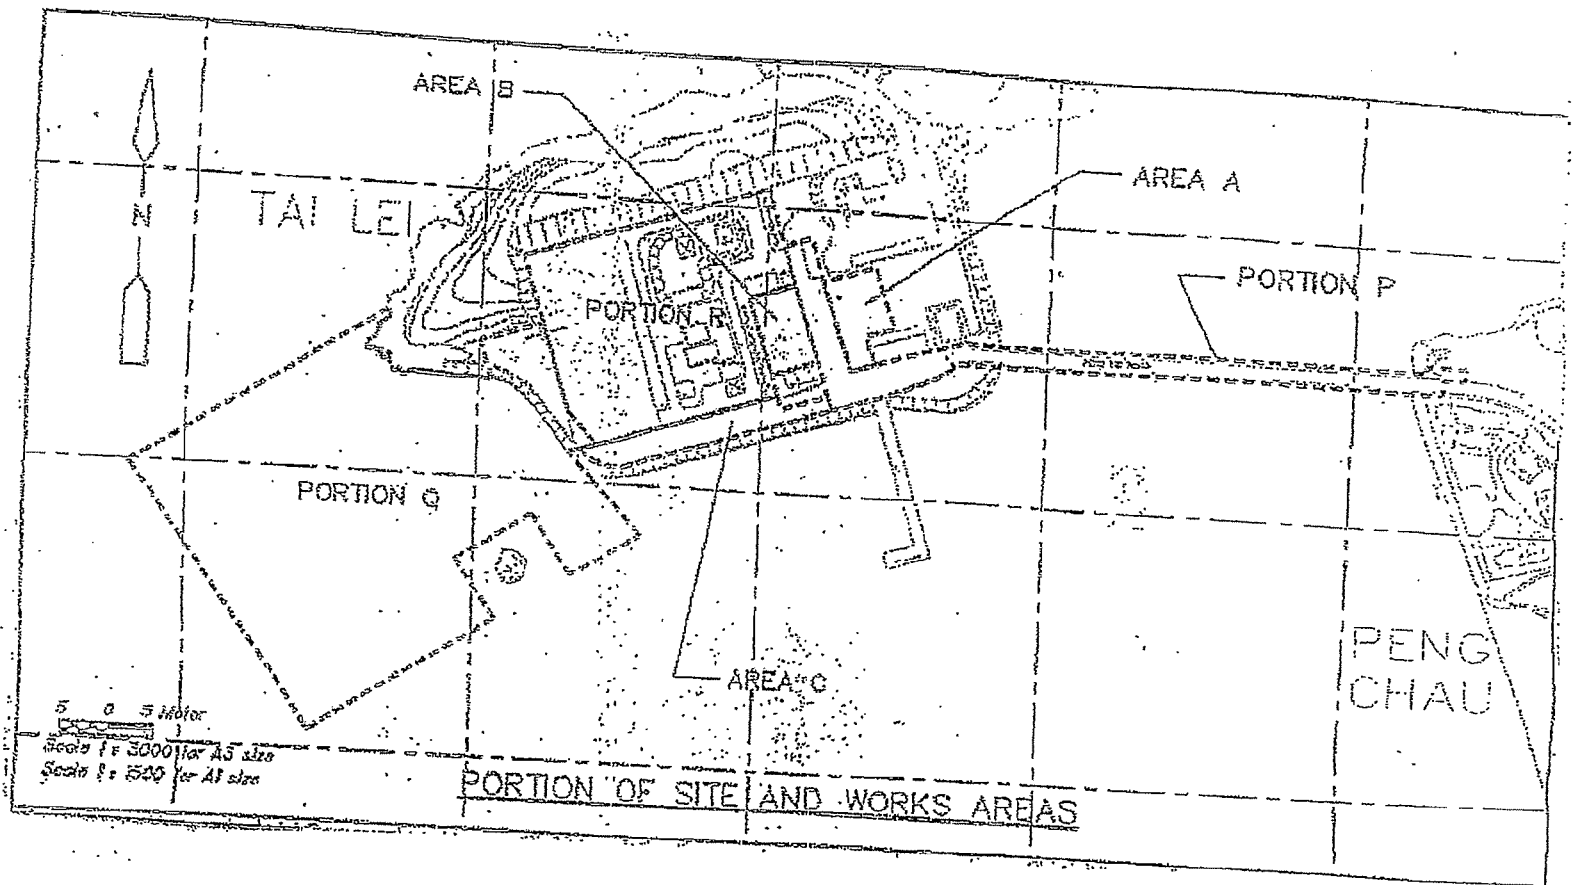

APPENDIX B


ENVIRONMENTAL ORGANIZATION STRUCTURE

Contact Details of Key Personnel

Organization	Project Role	Designation	Name of Key Staff	Tel No.	Fax No.
DSD	Employer	Permit Holder	Ir. David Leung	2594-7281	2827-8526
CDM	Engineer's Representative	Project Engineer	Ms. Angela Wong	2428-2332	2424-9114
		Resident Engineer	Mr. Samuel Tam	2983-9303	2983-9843
		ARE	Mr. Alex Yeung	2983-9303	2983-9843
BMT Asia	Independent Environmental Checker	IEC	Mr. Derek Ho	2815-2221	2815-3377
		IEC's Representative	Mr. K.C.Tse	2815-2221	2815-3377
Acciona-ATAL	Main Contractor	Project Manager	Mr. William Chan	2983-0092	2983-0381
		Site Agent	Mr. William Chan	2983-0092	2983-0381
AUES	Contractor's Environmental Team	Environmental Team Leader (ETL)	Mr. Ken Wong	2959-6059	2959-6079
		ETL's Representative	Miss. Sylvie Wong	2959-6059	2959-6079

APPENDIX C

LOCATIONS OF DESIGNATED MONITORING STATIONS

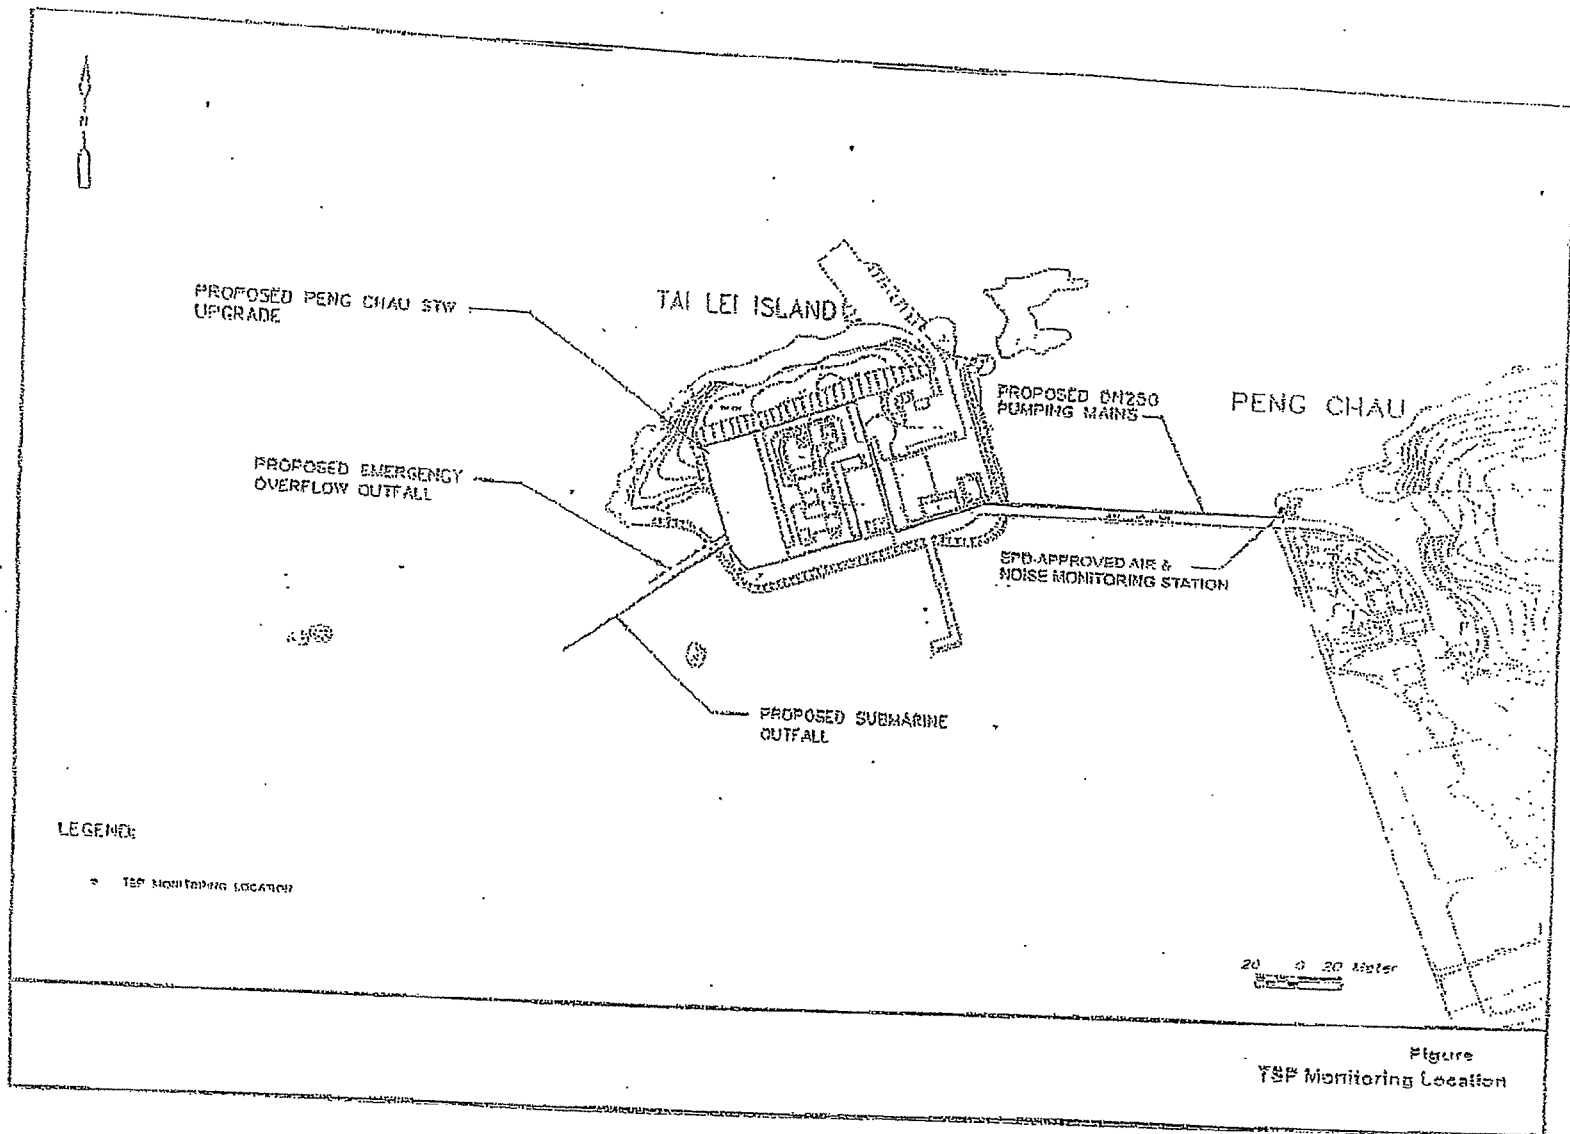

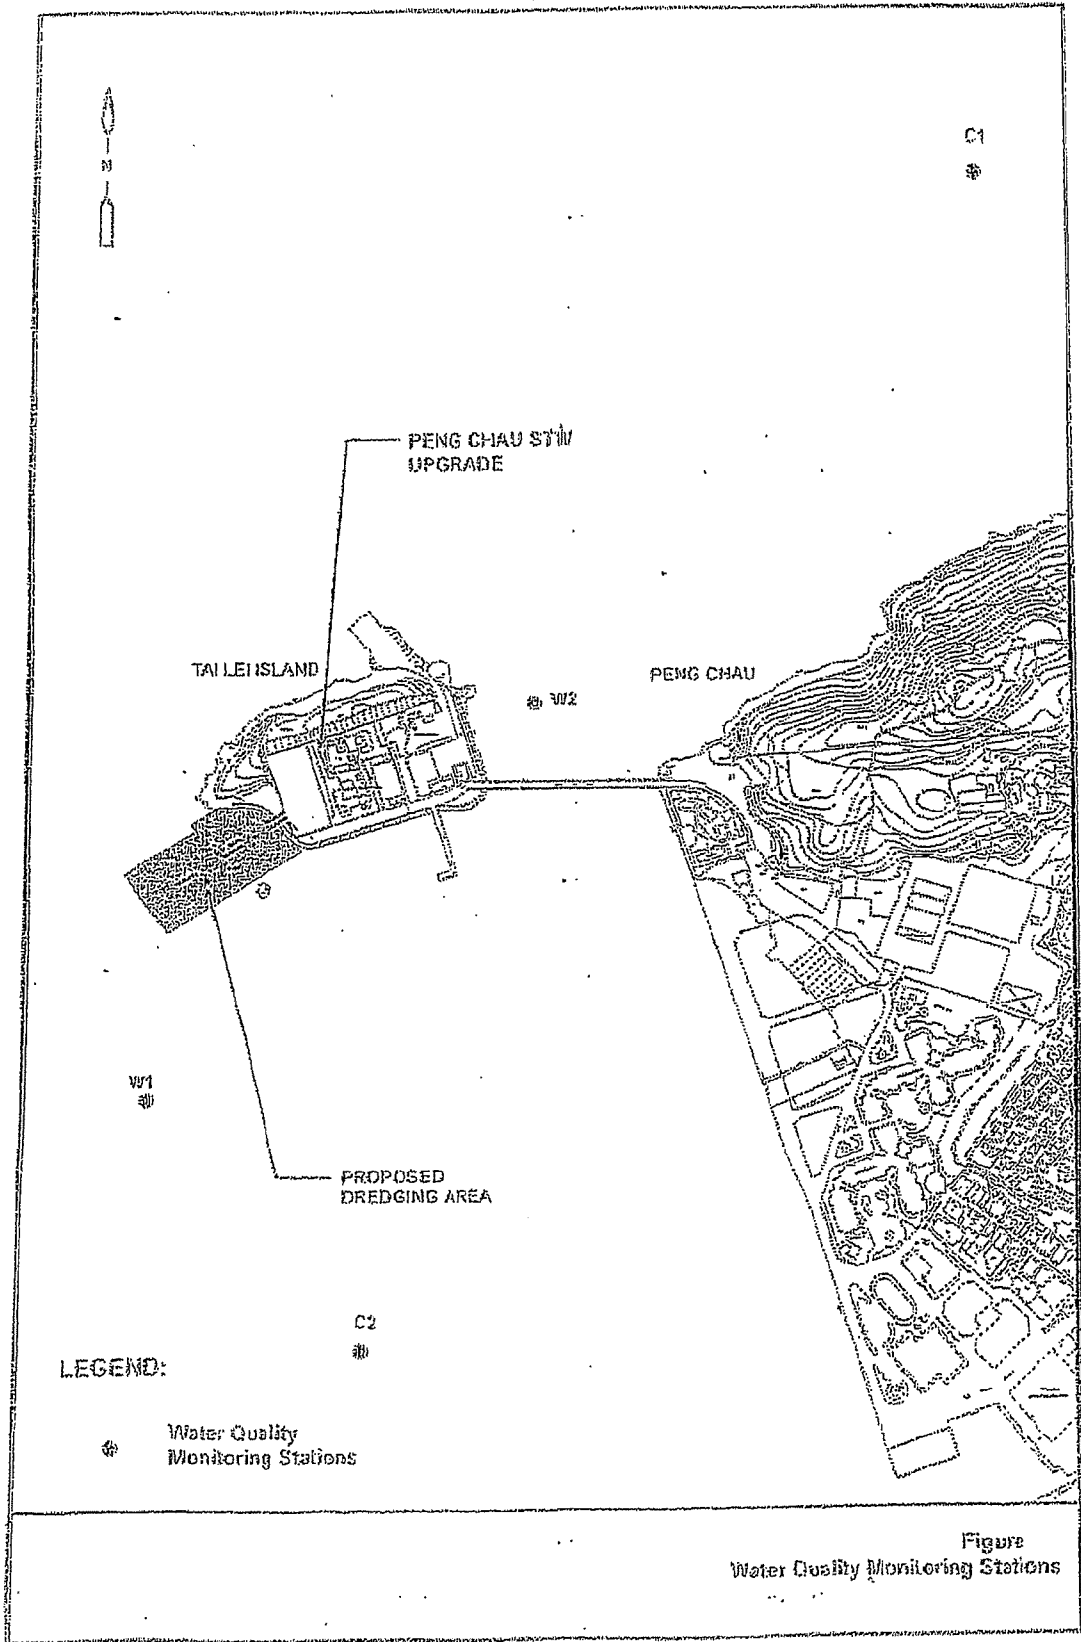


Figure
Water Quality Monitoring Stations

APPENDIX D

EQUIPMENT CALIBRATION CERTIFICATES

Equipment Calibration List for Peng Chau Sewage Treatment Works Upgrade Project

Item	Aspect	Description of Equipment	Serial No.	Date of Calibration	Date of Next Calibration
1*	Air	Greasby Anderson GMWS2310 High Volume Sampler	AN1	06 Aug 08	06 Nov 08
2		Sibata 8520 dust trap	23080	04 Sep 07	04 Sep 08
3	Noise	Bruel & Kjaer 4231 Acoustical Calibrator	2292167	22 Apr 08	22 Apr 09
4		Bruel & Kjaer 2238 Integrating Sound Level Meter	2285721	22 Apr 08	22 Apr 09

Note:* Calibration certificates will only be provided if monitoring equipment is re-calibrated or new.

No marine water quality impact monitoring was required in this reporting period, since all marine based construction activities were completed on 01 August 2006. Post marine water quality monitoring was carried out from 02 August to 01 September 2006. Therefore, no water quality monitoring equipments calibration certificate was enclosed in this Monthly EM&A Report.

APPENDIX E

IMPACT MONITORING SCHEDULES

Impact Monitoring Schedules in this Reporting Month

Date		Air Quality		Noise Monitoring
		1-Hour TSP	24-Hour TSP	
1-August-08	Fri			
2-August-08	Sat			
3-August-08	Sun			
4-August-08	Mon			
5-August-08	Tue			
6-August-08	Wed			
7-August-08	Thu			
8-August-08	Fri			
9-August-08	Sat			
10-August-08	Sun			
11-August-08	Mon			
12-August-08	Tue			
13-August-08	Wed			
14-August-08	Thu			
15-August-08	Fri			
16-August-08	Sat			
17-August-08	Sun			
18-August-08	Mon			
19-August-08	Tue			
20-August-08	Wed			
21-August-08	Thu			
22-August-08	Fri			
23-August-08	Sat			
24-August-08	Sun			
25-August-08	Mon			
26-August-08	Tue			
27-August-08	Wed			
28-August-08	Thu			
29-August-08	Fri			
30-August-08	Sat			
31-August-08	Sun			




	Monitoring Day
	Sunday or Public Holiday

No Water Quality Monitoring was required in this reporting period, since all marine based construction activities were completed on 01 August 2006. Post Water Quality was carried out from 02 August to 01 September 2006, monitoring results were presented in the previous Monthly EM&A Report (September 2006)

APPENDIX F

GRAPHICAL PLOTS OF AIR QUALITY AND CONSTRUCTION NOISE MONITORING RESULTS

Monthly Environmental Monitoring and Audit (EM&A) Report for August 2008

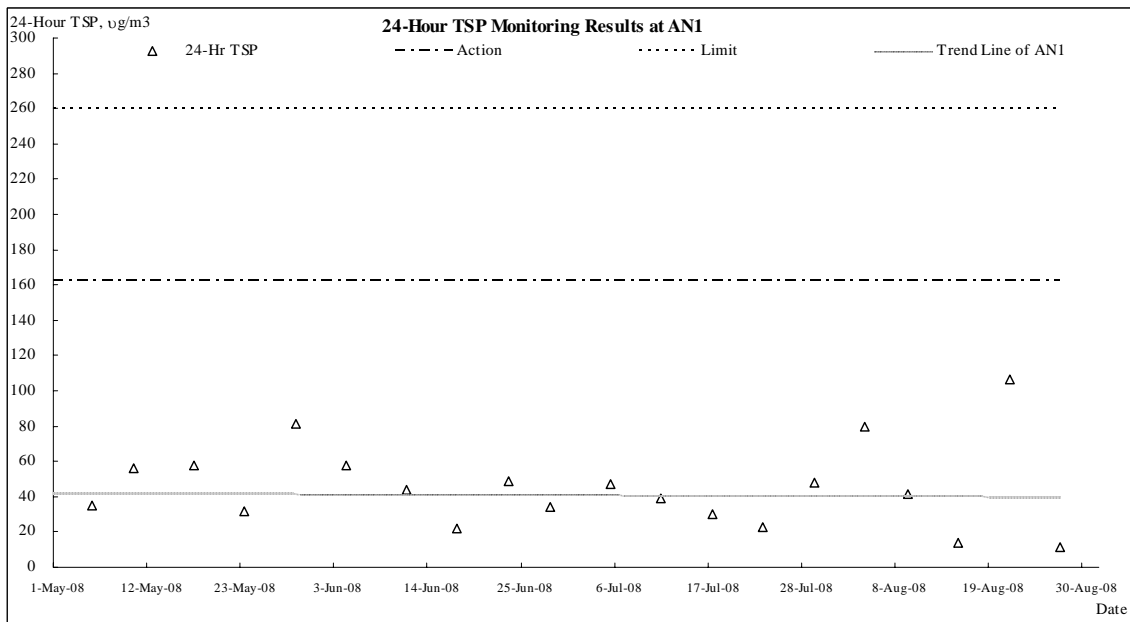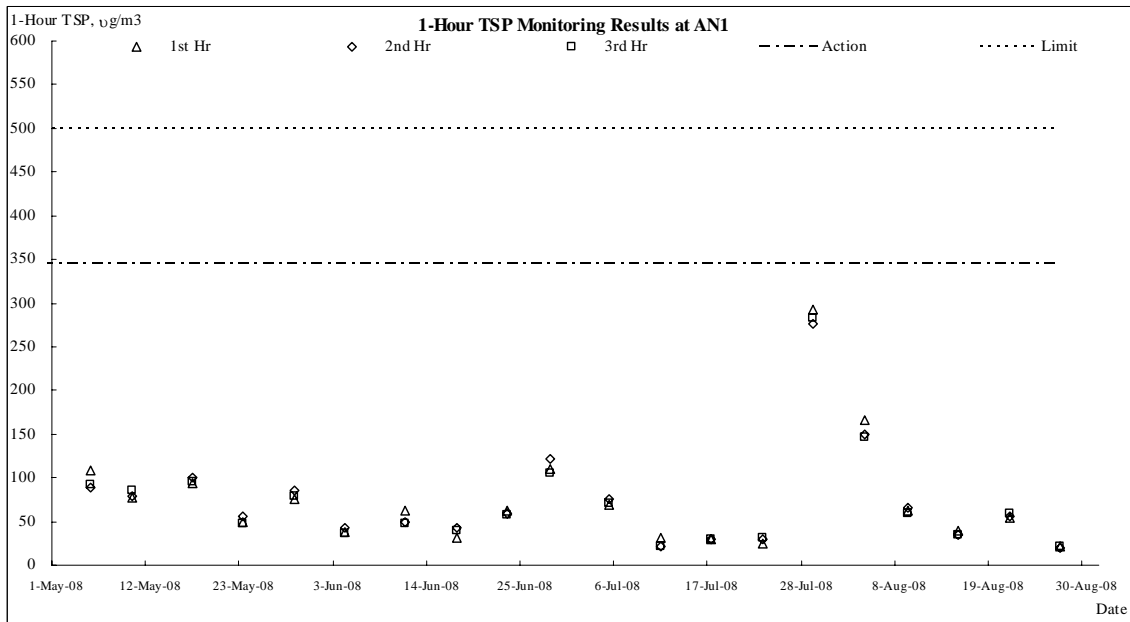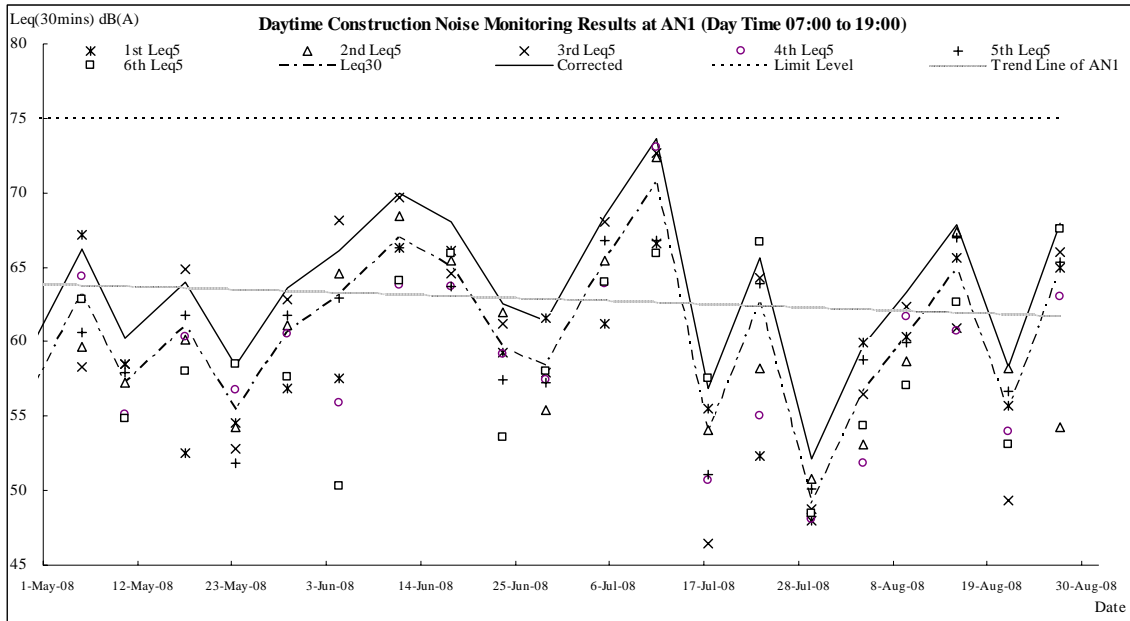

APPENDIX G

METEOROLOGICAL DATA IN THE REPORTING MONTH

Meteorological Data Extracted from HKO in the Reporting Month

Date		Weather	Peng Chau Weather Station				
			Total Rainfall (mm)	Means Air Temperature (°C)	Wind Speed (km/h)	Mean Relative Humidity (%)	Wind Direction
1-Aug-08	Fri	sunny periods/showers/fine/moderate	Trace	28.3	11.5	84	E/NE
2-Aug-08	Sat	fine/hot/moderate	Trace	28.9	9	83	E/NE
3-Aug-08	Sun	fine/very hot/moderate	0	28.9	8	78.5	S/SE
4-Aug-08	Mon	fine/very hot/isolated showers/moderate	Trace	29.2	8	84.5	NW
5-Aug-08	Tue	cloudy/squally showers/fresh	6.1	26.3	16	79.5	N/NW
6-Aug-08	Wed	No.8 Southeast Gale Of Storm Signal					
7-Aug-08	Thu	cloudy/squally showers/fresh	72.3	25.6	37.5	94.5	E
8-Aug-08	Fri	cloudy/scattered showers/squally thunderstorm/moderate	48.3	25.9	18.5	93.7	E/NE
9-Aug-08	Sat	cloudy/isolated showers/moderate	0	27.5	12	89	E/NE
10-Aug-08	Sun	cloudy/isolated showers/moderate	0	27.2	8	89	S/SW
11-Aug-08	Mon	cloudy/rain/squally thunderstorm/moderate	17.7	24.8	6	97	E/SE
12-Aug-08	Tue	fine/isolated showers/moderate	Trace	27.7	7.5	93.7	E/SE
13-Aug-08	Wed	fine/hot/moderate	0	29	7	89.5	SE
14-Aug-08	Thu	fine/hot/moderate	0	29	9	86.5	SW
15-Aug-08	Fri	fine/hot/moderate/fresh	0	28.7	9	87.5	S/SW
16-Aug-08	Sat	fine/hot/moderate/fresh	0	29.1	9.7	86.5	S/SW
17-Aug-08	Sun	fine/hot/showers/moderate	Trace	29.3	7.5	88.5	S/SSE
18-Aug-08	Mon	fine/hot/showers/moderate	Trace	29.2	7	88.5	E/SE
19-Aug-08	Tue	fine/very hot/moderate	Trace	29.4	9.5	86	E/SE
20-Aug-08	Wed	fine/very hot/isolated showers/light winds	0	29.9	8.2	86.5	S/SW
21-Aug-08	Thu	cloudy/scattered showers/squally thunderstorm/moderate	Trace	29.8	10	82.5	E/NE
22-Aug-08	Fri	increasing Gale Or Storm Signal No. 9					
23-Aug-08	Sat	cloudy/squally showers/fresh/strong	36.9	24.6	35.5	96.2	SW
24-Aug-08	Sun	fine/hot/moderate	Trace	27	6	90	S/SE
25-Aug-08	Mon	fine/hot/moderate	Trace	28.7	9	93	S/SE
26-Aug-08	Tue	fine/very hot/light winds	0	28.6	7.2	91.2	S/SE
27-Aug-08	Wed	fine/hot/moderate	0	28.7	6	88.2	S/SW
28-Aug-08	Thu	fine/hot/isolated showers/moderate	0	29.1	6.5	87.5	S/SW
29-Aug-08	Fri	fine/hot/isolated showers/moderate	0	29.4	7.5	Maintenance	S/SW
30-Aug-08	Sat	fine/hot/isolated showers/moderate	0	29.8	6	68.2	S/SW
31-Aug-08	Sun	fine/very hot/moderate	0	29.2	7.5	63	S/SW

APPENDIX H

THREE-MONTH ROLLING PROGRAM

Drainage Services Department
Contract No. DC/2004/08
Upgrading of Peng Chau Sewage Treatment Works
3-Months Rolling Programme (August 2008 to September 2008)

ID	Task Name	Duration	Start	Finish	2005												2006												2007												2008											
					4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9						
77	Section II - Portion R (STC & ESC)	1057 days	1/7/05	2/9/08	[Gantt bar from 2005-07 to 2008-09]																																															
102	Super-Structure works (forms, steel fixing and concrete casting)	794 days	10/5/06	2/9/08	[Gantt bar from 2006-05 to 2008-09]																																															
129	External wall painting at NSTC ((GLA/1-7, GLA-J/7, GLJ/2-7)	65 days	28/10/07	2/1/08	[Gantt bar from 2007-10 to 2008-01]																																															
130	External wall painting at NSTC (GL1/A-J)	30 days	4/8/08	2/9/08	[Gantt bar from 2008-08 to 2008-09]																																															
131	Demolition of tower crane	3 days	13/12/07	15/12/07	[Gantt bar from 2007-12 to 2007-12]																																															
132	Section III of Works	913 days	29/4/05	20/2/08	[Gantt bar from 2005-04 to 2008-02]																																															
133	Handover of Portion R	0 days	29/4/05	29/4/05	[Milestone diamond at 2005-04]																																															
134	Demolish Temporary Pump Pits & Reinstatement in Portion S	78 days	3/12/07	20/2/08	[Gantt bar from 2007-12 to 2008-02]																																															
135	Section IV of Works	1120 days	29/4/05	14/9/08	[Gantt bar from 2005-04 to 2008-09]																																															
136	Handover of Portion R	0 days	29/4/05	29/4/05	[Milestone diamond at 2005-04]																																															
137	Utility diversion (VO no.13 refers)	28 days	23/11/07	20/12/07	[Gantt bar from 2007-11 to 2007-12]																																															
138	Demolish Existing Facilities in Portion R (Claim No. 47 refers)	45 days	19/12/07	3/2/08	[Gantt bar from 2007-12 to 2008-02]																																															
139	Construction of Dry Bed House	224 days	4/2/08	14/9/08	[Gantt bar from 2008-02 to 2008-09]																																															
140	Excavation & formation	18 days	4/2/08	21/2/08	[Gantt bar from 2008-02 to 2008-02]																																															
141	Substructure	21 days	22/2/08	13/3/08	[Gantt bar from 2008-02 to 2008-03]																																															
142	Superstructure (Add 30 days EOT related to VO no.17)	60 days	14/3/08	12/5/08	[Gantt bar from 2008-03 to 2008-05]																																															
143	Finishes	21 days	13/5/08	2/6/08	[Gantt bar from 2008-05 to 2008-06]																																															
144	Glazing Panels	111 days	13/5/08	31/8/08	[Gantt bar from 2008-05 to 2008-08]																																															
145	Handover to E&M Works	0 days	2/6/08	2/6/08	[Milestone diamond at 2008-06]																																															
146	E&M Works	105 days	2/6/08	14/9/08	[Gantt bar from 2008-06 to 2008-09]																																															
147	All Drainage, Road (EVA) Construction & Landscape Works (including VO. No.13, No.17, 18)	135 days	3/5/08	14/9/08	[Gantt bar from 2008-05 to 2008-09]																																															

Project: Peng Chau-3months
Date: 1/9/08

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks			
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			
