



Monthly EM&A Report (October 2023)

0185/21/ED/585 01

Sai O Trunk Sewer Sewage Pumping Station

Ref.: SHKSOSPSEM00_0_0098L.23

14 November 2023

By Fax (2827 0485)

Sun Hung Kai Properties Ltd.
42/F., Sun Hung Kai Centre
30 Harbour Road, Wan Chai, Hong Kong

Attention: Mr. Sunny Cheung

Dear Sir,

**Re: Sai O Trunk Sewer Sewage Pumping Station
Environmental Permit No. EP-597/2021
Monthly EM&A Report (October 2023)**

Reference is made to the Environmental Team's submission of the Monthly EM&A Report for October 2023 (ET's ref.:0185/21/ED/0585 01) certified by the ET Leader and provided to us via e-mail on 10 November 2023.

We are pleased to inform you that we have no further comments on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 of EP-597/2021 and Section 12.4.1.1 of EM&A Manual for the captioned project.

Thank you very much for your attention and please feel free to contact the undersigned should you require further information.

Yours sincerely,
For and on behalf of
Ramboll Hong Kong Ltd.



Y H Hui
Independent Environmental Checker

c.c.	AECOM	Ms. Janice Tam / Mr. CK Man	(By Fax: 3894 5801)
	Fugro	Mr. Calvin Leung	(By Fax: 2450 6138)
	SGJV	Mr. Eddie Tse	(By Fax: 3894 5801)

Q:\Projects\SHKSOSPSEM00\02 Proj_Mgt\02 Corr\SHKSOSPSEM00_0_0098L.23.docx

Document Control

Document Information

Project Title	Sai O Trunk Sewer Sewage Pumping Station
Document Title	Monthly EM&A Report (October 2023)
Fugro Project No.	0185/21
Fugro Document No.	0185/21/ED/585 01
Issue Number	01

Client Information

Client	Light Time Investments Limited
Client Address	42/F, Sun Hung Kei Centre, 30 Harbour Road, Wan Chai, Hong Kong
Client Contact	Mr. Sunny Cheung

Environmental Team

Initials	Name	Role	Signature
MP	Calvin M.P. Leung	Environmental Team Leader	
KH	Toby K.H. Wan	Environmental Consultant	
CN	Calvin C.N. Poon	Environmental Consultant	

EXECUTIVE SUMMARY

- i. This Monthly Environmental Monitoring and Audit (EM&A) Report is prepared for Sai O Trunk Sewer Sewage Pumping Station. Light Time Investments Limited has appointed Fugro Technical Services Limited (FTS) to undertake the Environmental Team services for the project and implement the EM&A works.
- ii. This is the 21st Monthly EM&A Report for the Project which summaries findings of the EM&A programme during the reporting period from 1st October 2023 to 31st October 2023.

Breaches of Environmental Quality Performance Limits (Action & Limit levels)

- iii. No Action and Limit Level exceedance was recorded for air quality and construction noise monitoring in the reporting month.
- iv. No corrective actions were required according to the Event-Action Plans.

Complaint Log

- v. No complaints were received in the reporting period.

Notifications of any Summons and Successful Prosecutions

- vi. No notifications of summons and prosecutions were received in the reporting period.

Reporting Change

- vii. There were no reporting changes during the reporting month

Future Key Issues

- viii. The main works will be anticipated in the next month are as follow:

ABWF Works

- Interior finish – pump room
- Exterior and roof finish
- External works

E&M Works and OP

- CLP works – transformer room
- E&M works – pump room below and above ground
- E&M works - external

Contents

1.	INTRODUCTION	8
1.1	Background	8
1.2	Project Organization	9
1.3	Construction Programme and Activities	10
1.4	Works undertaken during the month	10
1.5	Status of Environmental Licences, Notification and Permits	11
2.	AIR QUALITY	12
2.1	Monitoring Requirement	12
2.2	Monitoring Equipment	12
2.3	Monitoring Parameters and Frequency	12
2.4	Monitoring Methodology	13
2.5	Maintenance and Calibration	14
2.6	Monitoring Locations	14
2.7	Monitoring Results	14
3.	NOISE	16
3.1	Monitoring Requirement	16
3.2	Monitoring Equipment	16
3.3	Monitoring Parameters and Frequency	16
3.4	Monitoring Methodology	17
3.5	Maintenance and Calibration	17
3.6	Monitoring Locations	18
3.7	Monitoring Results	18
3.8	Comparison of Noise Monitoring data with EIA Predictions	19
4.	SITE INSPECTION AND AUDIT	20
4.1	Site Inspection	20
4.2	Advice on the Solid and Liquid Waste Management Status	20
5.	NON-COMPLIANCE, COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS	21
5.1	Non-compliance (Exceedances of AL levels)	21
5.2	Complaints, Notification of Summons and Prosecution	21
6.	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURE	22
6.1	Implementation Status	22
7.	FUTURE KEY ISSUES	23
7.1	Construction Programme for the Next Month	23
7.2	Key Issues for the Coming Month	23
7.3	Monitoring Schedules for the Next Month	23

8.	CONCLUSION AND RECOMMENDATION	24
8.1	Conclusions	24
8.2	Comment and Recommendations	24

Tables

Table 1.1	Contact Information of Key Personnel
Table 1.2	Environmental Licenses, Notification and Permits Summary
Table 2.1	Air Quality Monitoring Equipment
Table 2.2	Monitoring Parameters and Frequencies of Noise Monitoring
Table 2.3	Air Quality Monitoring Locations
Table 2.4	Summary of Air Quality Monitoring Results
Table 3.1	Construction Noise Monitoring Equipment
Table 3.2	Monitoring Parameters and Frequencies of Noise Monitoring
Table 3.3	Construction Noise Monitoring Location
Table 3.4	Summary of Construction Noise Monitoring Results
Table 3.5	Comparison of Noise monitoring data with EIA predictions

Figures

Figure 1.1 Location of the proposed Sai O Trunk Sewer SPS

Figure 2.1 Air Quality Monitoring Location

Figure 3.1 Noise Monitoring Locations

Appendices

Appendix A Project Organization Chart

Appendix B Construction Programme

Appendix C Equipment Calibration Certificates

Appendix D Environmental Monitoring Schedule

Appendix E Air Quality & Construction Noise Monitoring Results

Appendix F Air Quality & Construction Noise Monitoring Graphs

Appendix G Action and Limit Level

Appendix H Event and Action Plan

Appendix I Weather and Meteorological Conditions during Reporting Month

Appendix J Wind Data

Appendix K Summary of Site Environmental Audit in the Reporting Month

Appendix L Waste Flow Table

Appendix M Cumulative Statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions

Appendix N Implementation Status of Environment Mitigation Measures (Construction Phase)

Appendix O Outstanding Issues and Deficiencies

1. INTRODUCTION

1.1 Background

- 1.1.1 The proposed Sai O Trunk Sewer Sewage Pumping Station (Sai O Trunk Sewer SPS) is a part of Public Works Programme Item 4125DS - Tolo Harbour Sewerage of Unsewered Areas, Stage II, is a core component of the proposed trunk sewerage system in Ma On Shan along Sai Sha Road. It is required to receive all sewage flows along Sai Sha Road from Kei Ling Ha Lo Wai to Cheung Muk Tau and the adjacent residential development, health care institution and education institutions, and then convey the sewage to Sha Tin Sewage Treatment Works.
- 1.1.2 Based on the latest design, the installed capacity per day of the proposed Sai O Trunk Sewer SPS is about 20,600m³ for coping with the sewerage needs of both existing and future developments. Location of the proposed Sai O Trunk Sewer SPS is shown in **Figure 1.1**.
- 1.1.3 The proposed Sai O Trunk Sewer SPS include the following main components:
- Loading/unloading bay
 - Inlet chamber
 - Coarse screen channel
 - Distribution chamber
 - Wet wells
 - Valve chamber
 - Emergency storage tank
 - Deodorizing unit
 - Switch room
 - Transformer room
- 1.1.4 The Project is a designated project under Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO) (Cap. 499) for which Environmental Impact Assessment (EIA) report and Environmental Monitoring and Audit (EM&A) Manual was approved by EPD (Register No.: AEIAR-230/2021) on 4 June 2021. The Environmental Permit (EP) (EP No. EP-597/2021) was issued by EPD on 28 September 2021.
- 1.1.5 Fugro Technical Services Limited (FTS) has been appointed as the Environmental Team (ET) by Light Time Investments Limited to undertake the Environmental Team services for the Project and implement the EM&A works under Sai O Trunk Sewer Sewage Pumping Station (hereinafter referred as “the Project”).

- 1.1.6 This is the 21st Monthly EM&A report to document the findings of site inspection activities and EM&A programme for this project from 1st October 2023 to 31st October 2023 (reporting period) and is submitted to fulfil Condition 3.4 of the EP and Section 12.4 of the EM&A Manual. According to Condition 4 of the EP, electronic reporting is provided on the internet website to facilitate public inspection of the report.

1.2 Project Organization

- 1.2.1 The Project Organization structure is shown in **Appendix A**. The key personnel contact names and numbers are summarized in **Table 1.1**.

Table 1.1 – Contact Information of Key Personnel

Party	Position	Name	Telephone
Project Proponent (PP) (Light Time Investments Ltd.)	Senior Project Manager	Mr. Sunny Cheung	3894 5934
Engineer's Representative (ER) (AECOM Asia Co. Ltd.)	Senior Resident Engineer	Mr. C.K. Man	3894 5919
Independent Environmental Checker (IEC) (Ramboll Hong Kong Ltd.)	Independent Environmental Checker	Mr. Y.H. Hui	3465 2888
Contractor (Sanfield-Gammon Construction JV Company Ltd.)	Environmental Officer	Ms. Carrie Kwan	3894 5816
Environmental Team (ET) (Fugro Technical Services Ltd.)	Environmental Team Leader (ETL)	Mr. Calvin Leung	3565 4441

1.3 Construction Programme and Activities

1.3.1 The construction programme of this project is shown in **Appendix B**.

1.4 Works undertaken during the month

1.4.1 Major construction activities were undertaken in the reporting month were:

ABWF Works

- Interior finish – pump room
- Exterior and roof finish
- External works

E&M Works and OP

- CLP works – transformer room
- E&M works – pump room below and above ground

1.5 Status of Environmental Licences, Notification and Permits

- 1.5.1 A summary of the relevant permits, licenses and/or notifications on environmental protection for this project is presented in **Table 1.2**.

Table 1.2 – Environmental Licenses, Notification and Permits Summary

Permit/ Notification/ License	Reference No	Valid From	Valid Till
Environmental Permit	EP-597/2021	28-Sep-2021	NA
Notification of Construction Works under APCO	494463	18-Apr-2018	31-Dec-2024
Billing Account under Construction Waste Disposal Charging Scheme	7031695	28-Aug-2018	NA
Effluent Discharge License under WPCO	WT00040139-2021	11-Mar-2022	31-Mar-2027
Chemical Waste Producer Registration	8334-741-S4115-01	14-Aug-2018	NA
Construction Noise Permit	GW-RN0867-23	14-Aug-2023	13-Dec-2023

Notes:

NA = Not Applicable

2. AIR QUALITY

2.1 Monitoring Requirement

- 2.1.1 In accordance with the EM&A Manual, 1-hour Total Suspended Particulates (TSP) levels should be measured at the designated air quality monitoring station to ensure that any deteriorating air quality could be readily detected and timely action shall be undertaken to rectify such situation. Impact 1-hour TSP monitoring was conducted for at least three times every 6 days when the highest dust impact occurs.

2.2 Monitoring Equipment

- 2.2.1 1-hour TSP air quality monitoring was performed using High Volume Sampler (HVS) deployed at the designated monitoring station. The HVS shall meet all the requirements of the EM&A Manual.
- 2.2.2 Wind data monitoring equipment is provided at the conspicuous locations for logging wind speed and wind direction near to the air quality monitoring location. The equipment installation location is agreed with the ER and the IEC.
- 2.2.3 The model of the air quality monitoring equipment used is summarized in **Table 2.1**.

Table 2.1 – Air Quality Monitoring Equipment

Item	Brand	Model	Equipment	Serial No.
1	Tisch	TE-5170 (TSP)	High Volume Sampler	HVS-05
		TE-300-310X	-Mass Flow Controller	3088
		TE-5005X	-Blower Motor Assembly	2083
		TE-5007X	-Mechanical Timer	5159
		TE-5009X	-Continuous Flow Recorder	5483
2	Global Water	GL500-7-2	Wind Station	WS-03
3	Tisch	TE-5025A	Calibration Kit	2456

2.3 Monitoring Parameters and Frequency

- 2.3.1 The parameters and frequencies of impact noise monitoring is summarized in **Table 2.2**.

Table 2.2 – Monitoring Parameters and Frequencies of Air Quality Monitoring

Parameter	Frequency
1-hour TSP	At least three times every 6 days when the highest dust impact occurs

2.4 Monitoring Methodology

HVS Installation

2.4.1 The following guidelines were adopted during the installation of HVS:

- i. A horizontal platform with appropriate support to secure the samplers against gusty wind shall be provided;
- ii. Two samplers shall be placed less than 2 meters apart;
- iii. The distance between the sampler and an obstacle, such as buildings, must be at least twice the height that the obstacle protrudes above the sampler;
- iv. A minimum of 2 metres of separation from walls, parapets and penthouses is required for rooftop samplers;
- v. A minimum of 2 metres of separation from any supporting structure, measured horizontally is required;
- vi. No furnace or incinerator flue is nearby;
- vii. Airflow around the sampler is unrestricted;
- viii. The sampler is more than 20 metres from the dripline;
- ix. Any wire fence and gate, to protect the sampler, shall not cause any obstruction during monitoring;
- x. Permission must be obtained to set up the samplers and to obtain access to the monitoring stations; and
- xi. A secured supply of electricity is needed to operate the samplers.

Operating / Analytical Procedures

- 2.4.2 Prior to the commencement of the dust sampling, the flow rate of the HVS shall be properly set. The flow rate shall be indicated on the flow rate chart. The power supply should be checked to ensure the proper functioning of the sampler. The sampler is recommended to be operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air monitoring station.
- 2.4.1 The filter holding frame should be removed by loosening the four nuts and placing carefully a weighted and conditioned filter at the centre with the stamped number upwards on a supporting screen.
- 2.4.2 The filter should be aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. The filter holding frame should be tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.

- 2.4.3 A programmed timer should be used to control the duration of operation. Information should be recorded on the record sheet, which included the starting time, the weather condition and the filter number.
- 2.4.4 After sampling process is finished, the filter should be removed and sent to the laboratory for weighting. The elapsed time should also be recorded.
- 2.4.5 All filter papers should be equilibrated in a conditioning environment for 24 hours before weighting. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than $\pm 3^{\circ}\text{C}$; the relative humidity (RH) should be $< 50\%$ and not vary by more than $\pm 5\%$. A convenient working RH is 40%.

2.5 Maintenance and Calibration

- 2.5.1 The high-volume motors and their accessories should be properly maintained, including routine motor brushes replacement and electrical wiring checking, to ensure that the equipment and a continuous power supply were in good working condition.
- 2.5.2 Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bimonthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The calibration certificate for the HVS is provided in **Appendix C**.

2.6 Monitoring Locations

- 2.6.1 In accordance with the EM&A Manual, air quality monitoring should be carried out at a designated monitoring location.
- 2.6.2 As limitation of stable electricity supply & safety concern could not be obtained from the designated dust monitoring location, an alternative monitoring location (CA_M1(a)) was proposed to measure 1-hour TSP levels in accordance with EP Condition 3.1 & Section 2.2.1.20 of the EM&A manual. The alternative monitoring location (CA_M1(a)) was approved by EPD on 15 December 2021.
- 2.6.3 The air quality monitoring location summarised in **Table 2.3** and shown in **Figure 2.1**.

Table 2.3 – Air Quality Monitoring Locations

Monitoring Location ID	Location
CA_M1(a)	Construction Site Boundary near Hong Kong Baptist Theological Seminary (HKBTS) Staff & Students Quarters

2.7 Monitoring Results

- 2.7.1 The schedule of air quality monitoring in reporting month is provided in **Appendix D**.
- 2.7.2 The monitoring data of 1-hr TSP are summarized in **Table 2.4**. The Detailed air quality monitoring results & graphs are presented in **Appendix E** & **Appendix F** respectively.

Table 2.4 – Summary of Air Quality Monitoring Results

Monitoring Station	Average ($\mu\text{g}/\text{m}^3$)	Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
1-hour TSP				
CA_M1(a)	102.9	36.3 – 178.4	339	500

- 2.7.3 No Action and Limit level exceedance was recorded in the reporting month.
- 2.7.4 No effect that arose from the other special phenomena and work progress of the concerned site was noted during the current monitoring month.
- 2.7.5 The Action and Limit Levels for impact air quality monitoring have been set and are presented in **Appendix G**.
- 2.7.6 The Event and Action Plan for Air Quality is given in **Appendix H**.
- 2.7.7 The weather conditions during the monitoring are provided in **Appendix I**.
- 2.7.8 The wind data obtained from the on-site wind station during the reporting period is provided in **Appendix J**.

3. NOISE

3.1 Monitoring Requirement

- 3.1.1 In accordance with the EM&A Manual, Leq (30min) monitoring is conducted at least once a week when there are Project-related construction activities being undertaken within a radius of 300 m from the monitoring stations. The monitoring is conducted during the construction phase between 0700 and 1900 on normal weekdays at the designated monitoring locations.

3.2 Monitoring Equipment

- 3.2.1 As referred to the requirements of the Technical Memorandum (TM) issued under the NCO, the sound level meters in compliance with the International Electro technical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications should be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement, the accuracy of the sound level meter should be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. The measurements may be accepted as valid only if the difference between calibration levels obtained before and after the noise measurement is less than 1.0 dB (94 dB \pm 0.1 dB).
- 3.2.2 The model of the noise monitoring equipment used is summarized in **Table 3.1**.

Table 3.1 – Construction Noise Monitoring Equipment

Item	Brand	Model	Equipment	Serial No.
1	Casella	CEL-63X Series	Integrating Sound Level Meter	1488269
2	Casella			4181568
3	Casella	CEL-120/1	Calibrator	2525896
4	Casella			4358250
5	Smart Sensor	AR816	Anemometer	AM-001

3.3 Monitoring Parameters and Frequency

- 3.3.1 The parameters and frequencies of impact noise monitoring is summarized in **Table 3.2**.

Table 3.2 – Monitoring Parameters and Frequencies of Noise Monitoring

Parameter	Frequency
L _{Aeq} (30 min) (L ₁₀ and L ₉₀ will be recorded for reference)	At each station at 0700-1900 hours on normal weekdays at a frequency of once a week when construction activities are underway

3.4 Monitoring Methodology

3.4.1 Noise measurement should be conducted as the following procedures:

- The monitoring station will set at a point 1m from the exterior of the sensitive receivers building façade and set at a position 1.2m above the ground. (In case façade measurement is not feasible on-site, a free field correction of +3dB(A) will be applied.)
- The battery condition was checked to ensure good functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time will set as follows:
 - frequency weighting: A
 - time weighting: Fast
 - measurement time: 30 minutes
- Prior to and after noise measurement, the meter shall be calibrated using the calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement is more than 1.0 dB, the measurement will be considered invalid and repeat of noise measurement is required after re-calibration or repair of the equipment.
- Noise measurement should be paused during periods of high intrusive noise if possible and observation shall be recorded when intrusive noise is not avoided.
- Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s. Calibration certificate of the anemometer is provided in **Appendix C**.

3.5 Maintenance and Calibration

3.5.1 Maintenance and calibration procedures should also be carried out, including:

- The microphone head of the sound level meter and calibrator should be cleaned with a soft cloth at quarterly intervals.
- The sound level meter and calibrator should be calibrated annually by a HOKLAS laboratory.
- Relevant calibration certificates are provided in **Appendix C**.

3.6 Monitoring Locations

3.6.1 In accordance with the EM&A Manual, noise monitoring should be carried out at 2 designated monitoring locations.

3.6.2 The noise monitoring locations are summarised in **Table 3.3** and shown in **Figure 3.1**.

Table 3.3 – Construction Noise Monitoring Location

Monitoring Location ID	Location	Measurements
CN_M1	In front of the HKBTs Staff & Students Quarters	Free Field
CN_M2	In front of the HKBTs Administration and Education Block	Façade

Note: Correction of +3 dB(A) shall be made to the free field measurements.

3.7 Monitoring Results

3.7.1 The schedule of noise monitoring in reporting month is provided in **Appendix D**.

3.7.2 The noise monitoring data are summarized in **Table 3.4**. The Detailed noise monitoring results & graphs are presented in **Appendix E** & **Appendix F** respectively.

Table 3.4 – Summary of Construction Noise Monitoring Results

Frequency and Period	Location	Corrected L _{Aeq}		Action Level	Limit Level
		Range (dB(A))	Average (dB(A))		
0700-1900 hours in normal weekdays LAeq (30min)	CN_M1	61.2 – 63.9	62.4	When one documented complaint is received	70dB(A) during normal teaching period and examination periods 65 dB(A) during
	CN_M2	54.7 – 58.9	57.3		

Remark:

1. CN_M1: Free-field measurement (+3 dB(A) correction has been applied).

3.7.3 No Action / Limit Level exceedance of location CN_M1 & CN_M2 was recorded for construction noise in the reporting month.

3.7.4 Construction Noise and Road traffic noise along Ning Ming Road was observed at CN_M1 & CN_M2 during the monitoring month. No effect that arose from the other special phenomena was noted during the current monitoring month.

3.7.5 The Action and Limit Levels for Construction Noise have been set and are presented in **Appendix G**.

3.7.6 The Event and Action Plan for Construction Noise is given in **Appendix H**.

3.7.7 No raining and wind with speed over 5 m/s was observed during noise monitoring according to the onsite observation. The weather conditions during the monitoring month are provided in **Appendix I**.

3.8 Comparison of Noise Monitoring data with EIA Predictions

3.8.1 The noise monitoring data was compared with the EIA predictions as summarized in **Table 3.5**.

Table 3.5 – Comparison of Noise monitoring data with EIA predictions

Monitoring Station	EIA ID	Maximum Predicted Mitigated Construction Noise Level L _{eq} (30min) dB(A)	Maximum Construction Noise Level in October 2023 L _{eq} (30min) dB(A)
CN_M1	N1b	72	63.9
CN_M2	N2	66	58.9

Notes:

Predicted Construction Noise Levels extracted from Table 4.8 of EIA Report, AEIAR-230/2021

3.8.2 The construction noise monitoring results at CN_M1 and CN_M2 were below the Maximum Predicted mitigated Construction Noise Level in the approved Environmental Impact Assessment (EIA) Report (Register No.: AEIAR-230/2021).

4. SITE INSPECTION AND AUDIT

4.1 Site Inspection

- 4.1.1 Site audits were carried out by ET on weekly basis to monitor the implementation of proper environmental management practices and mitigation measures in the Project site.
- 4.1.2 In the reporting month, 5 site inspections were carried out on 3, 9, 17, 24 and 31 October 2023.
- 4.1.3 No outstanding issues were reported during the reporting month. The Site Environmental Audit are summarized in **Appendix K**.

4.2 Advice on the Solid and Liquid Waste Management Status

- 4.2.1 The Contractor registered as a chemical waste producer for the Contract. Sufficient numbers of receptacles were available for general refuse collection and sorting.
- 4.2.2 The monthly summary of waste flow table is detailed in **Appendix L**.
- 4.2.3 If off-site disposal is required, the excavated marine mud from the land-based works shall be disposed of at the designated disposal sites within Hong Kong as allocated by the Marine Fill Committee or other locations as agreed by the Director. The Contractor shall ensure no spilling and overflowing of materials during loading / unloading / transportation is allowed.
- 4.2.4 The Contractor was reminded that chemical waste should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packing, Labelling and Storage of Chemical Waste.

5. NON-COMPLIANCE, COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS

5.1 Non-compliance (Exceedances of Action & Limit levels)

- 5.1.1 No Action and Limit Level exceedance was recorded for 1-hr TSP level at CA_M1(a) in the reporting month.
- 5.1.2 No Action / Limit Level exceedance was recorded for construction noise at CN_M1 & CN_M2 in the reporting month.

5.2 Complaints, Notification of Summons and Prosecution

- 5.2.1 No environmental complaint, notification of summons and successful prosecution were received in the reporting month.
- 5.2.2 Cumulative complaint log, summaries of complaints, notification of summons and successful prosecutions are presented in **Appendix M**.
- 5.2.3 No corrective actions were required.

6. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURE

6.1 Implementation Status

The Contractor had implemented environmental mitigation measures and requirements as stated in the EIA Report, the EP and EM&A Manual. **Appendix N** summarized the Implementation Status of Environment Mitigation Measures.

7. FUTURE KEY ISSUES

7.1 Construction Programme for the Next Month

ABWF Works

- Interior finish – pump room
- Exterior and roof finish
- External works

E&M Works and OP

- CLP works – transformer room
- E&M works – pump room below and above ground
- E&M works – external

7.2 Key Issues for the Coming Month

- 7.2.1 Potential environmental impacts arising from the above construction activities are mainly associated with construction dust, construction noise, waste management, and landscape and visual impact issues.

7.3 Monitoring Schedules for the Next Month

- 7.3.1 The tentative schedule for environmental monitoring in the coming month is provided in **Appendix D**.

8. CONCLUSION AND RECOMMENDATION

8.1 Conclusions

- 8.1.1 1-hour TSP impact monitoring was carried out in the reporting month. No Action and Limit Level exceedance was recorded in the reporting month.
- 8.1.2 Construction noise monitoring was carried out in the reporting month. No Action / Limit Level exceedance at CN_M1 & CN_M2 was recorded during the period.
- 8.1.3 Five environmental site inspections were carried out in the reporting month. Recommendations on mitigation measures for Permit/ Licenses were given to the Contractor for remediating the deficiencies identified during the site inspections.
- 8.1.4 Two landscape and visual site audits were carried out in the reporting month. Recommendations on mitigation measures for Permit/ Licenses were given to the Contractor for remediating the deficiencies identified during the site inspections.
- 8.1.5 Referring to the Contractor's information, no environmental complaint, notification of summons and successful prosecution was received in the reporting month.

8.2 Comment and Recommendations

- 8.2.1 The recommended environmental mitigation measures, as proposed in the EIA report and EM&A Manual shall be effectively implemented to minimize the potential environmental impacts from the Project. The EM&A programme would effectively monitor the environmental impacts generated from the construction activities and ensure the proper implementation of mitigation measures.

- 8.2.2 **According to the environmental site inspections performed in the reporting month, the following recommendations were provided:**

Air Quality Impact

- No specific observation was identified in the reporting month.

Construction Noise Impact

- No specific observation was identified in the reporting month.

Water Quality Impact

- No specific observation was identified in the reporting month.

Chemical Waste and Waste Management

- No specific observation was identified in the reporting month.

Landscape and Visual Impact

- No specific observation was identified in the reporting month.


Permit/ Licenses

- No specific observation was identified in the reporting month.

Figure 1.1

Location of the proposed Sai O Trunk
SPS

ISO A1 594mm x 841mm
Approved:
Checked:
Designer:
Project Management Initials:
Pld File by: ZHUNZ
2020/06/20
PATH: P:\Projects\6054728\Drawing\Report\A1EIA_721.dgn

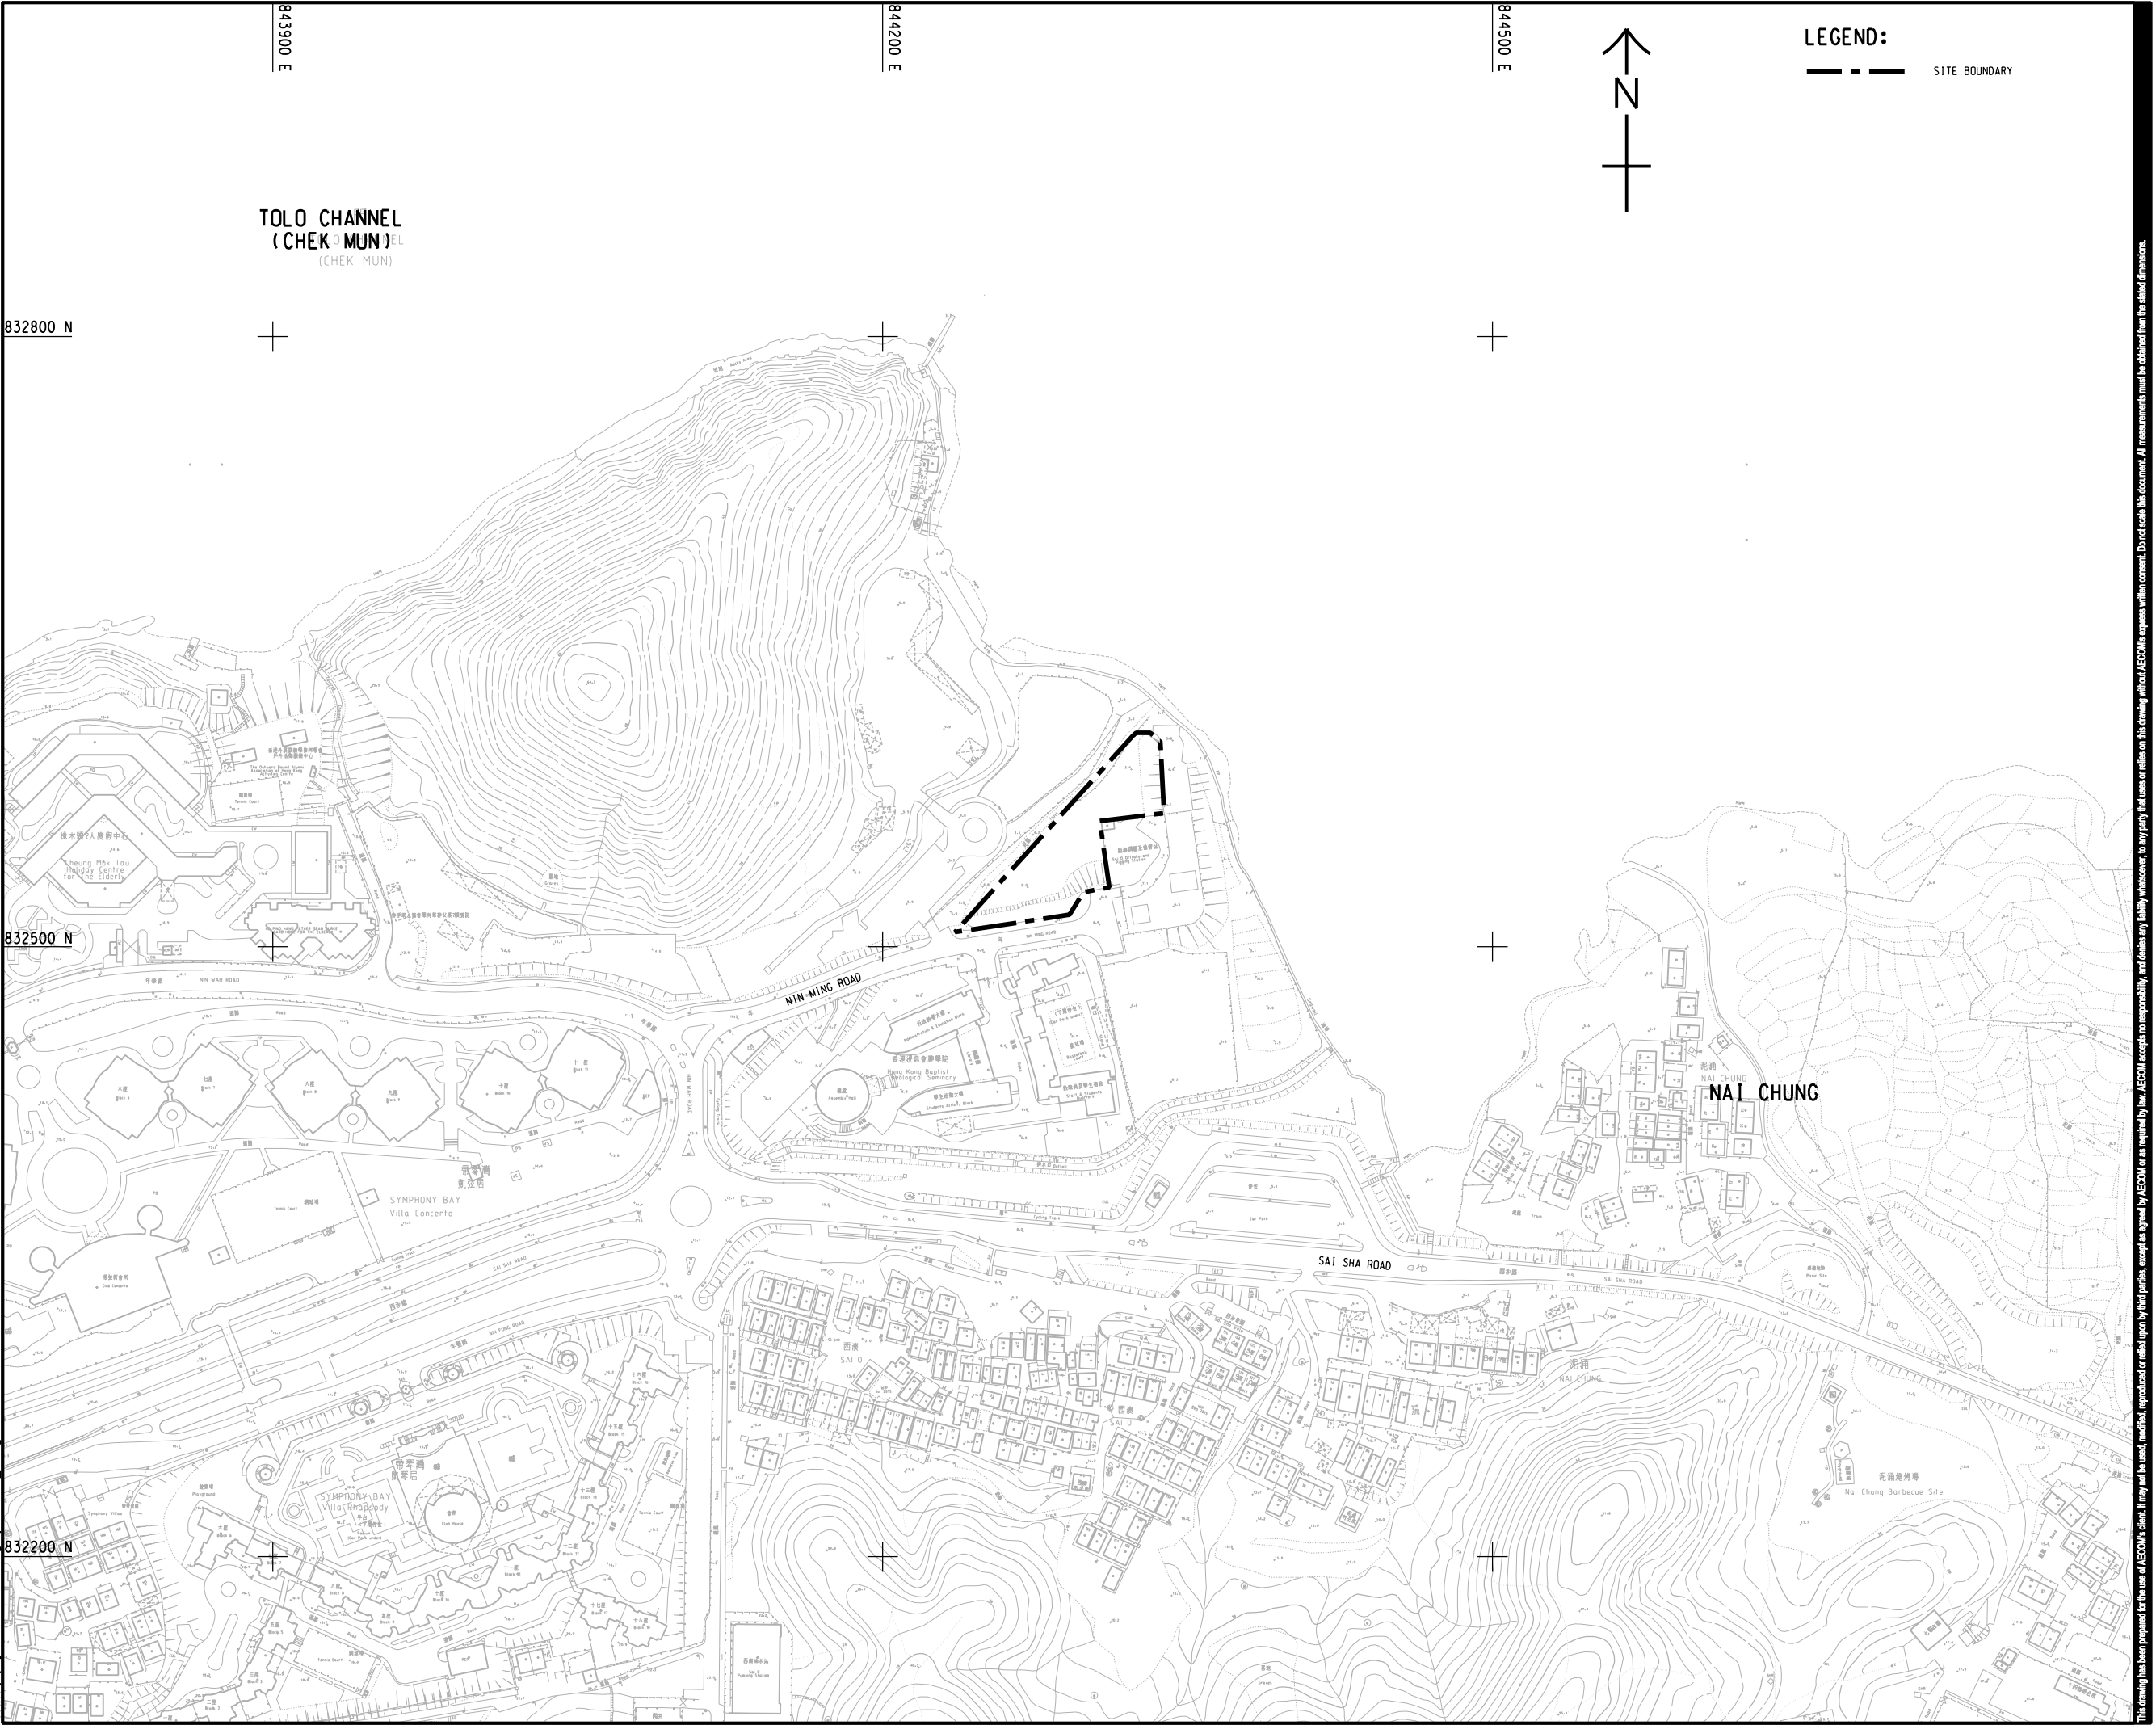

PROJECT
項目
**TOLO HARBOUR
SEWERAGE OF
UNSEWERED AREAS
STAGE 2 -
INVESTIGATION, DESIGN
AND CONSTRUCTION**

CLIENT
業主
 渠務署
Drainage Services Department

CONSULTANT
工程顧問公司
AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS
分判工程顧問公司

ISSUE/REVISION
修訂

I/R 修訂	DATE 日期	DESCRIPTION 內容摘要	CHK. 校核

STATUS
階段

SCALE
比例
A1 1: 1500

DIMENSION UNIT
尺寸單位
METRES

KEY PLAN
索引圖

PROJECT NO.
項目編號
60547289

CONTRACT NO.
合約編號

SHEET TITLE
圖紙名稱

**LOCATION OF THE PROPOSED
SAI O TRUNK SEWER SEWAGE
PUMPING STATION**

SHEET NUMBER
圖紙編號

60547289/EM&A/FIGURE 1.1

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party for loss or damage on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

Figure 2.1

Air Quality Monitoring Location

ISO A1 594mm x 841mm
Approved:
Checked:
Designer:
Project Management Initials:
Plot File by: ZHUJUNZ 2020/12/21
PATH P:\PROJECTS\60547289\DRAWING\Report\EA\EA_731.dgn



LEGEND:

- SITE BOUNDARY
- 500m ASSESSMENT AREA
- REPRESENTATIVE AIR SENSITIVE RECEIVER
- ✗ CA_M1(a) PROPOSED AIR QUALITY MONITORING POINT DURING CONSTRUCTION PHASE

AECOM

PROJECT
項目

TOLO HARBOUR SEWERAGE OF UNSEWERED AREAS STAGE 2 - INVESTIGATION, DESIGN AND CONSTRUCTION

CLIENT
業主

渠務署
Drainage Services Department

CONSULTANT
工程顧問公司

AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS
分判工程顧問公司

ISSUE/REVISION			
修訂			
IR	DATE	DESCRIPTION	CHK.
修訂	日期	修改描述	校核
STATUS			
校核			
SCALE		DIMENSION UNIT	
比例		單位	
A1 1 : 2000		METRES	
KEY PLAN			
索引圖			

PROJECT NO.
項目編號

60547289

CONTRACT NO.
合約編號

SHEET TITLE
圖紙名稱

LOCATIONS OF PROPOSED DUST MONITORING POINT

SHEET NUMBER
圖紙編號

60547289/EM&A/FIGURE 2.1


This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

Figure 3.1

Noise Monitoring Locations

Appendix A

Project Organization Chart

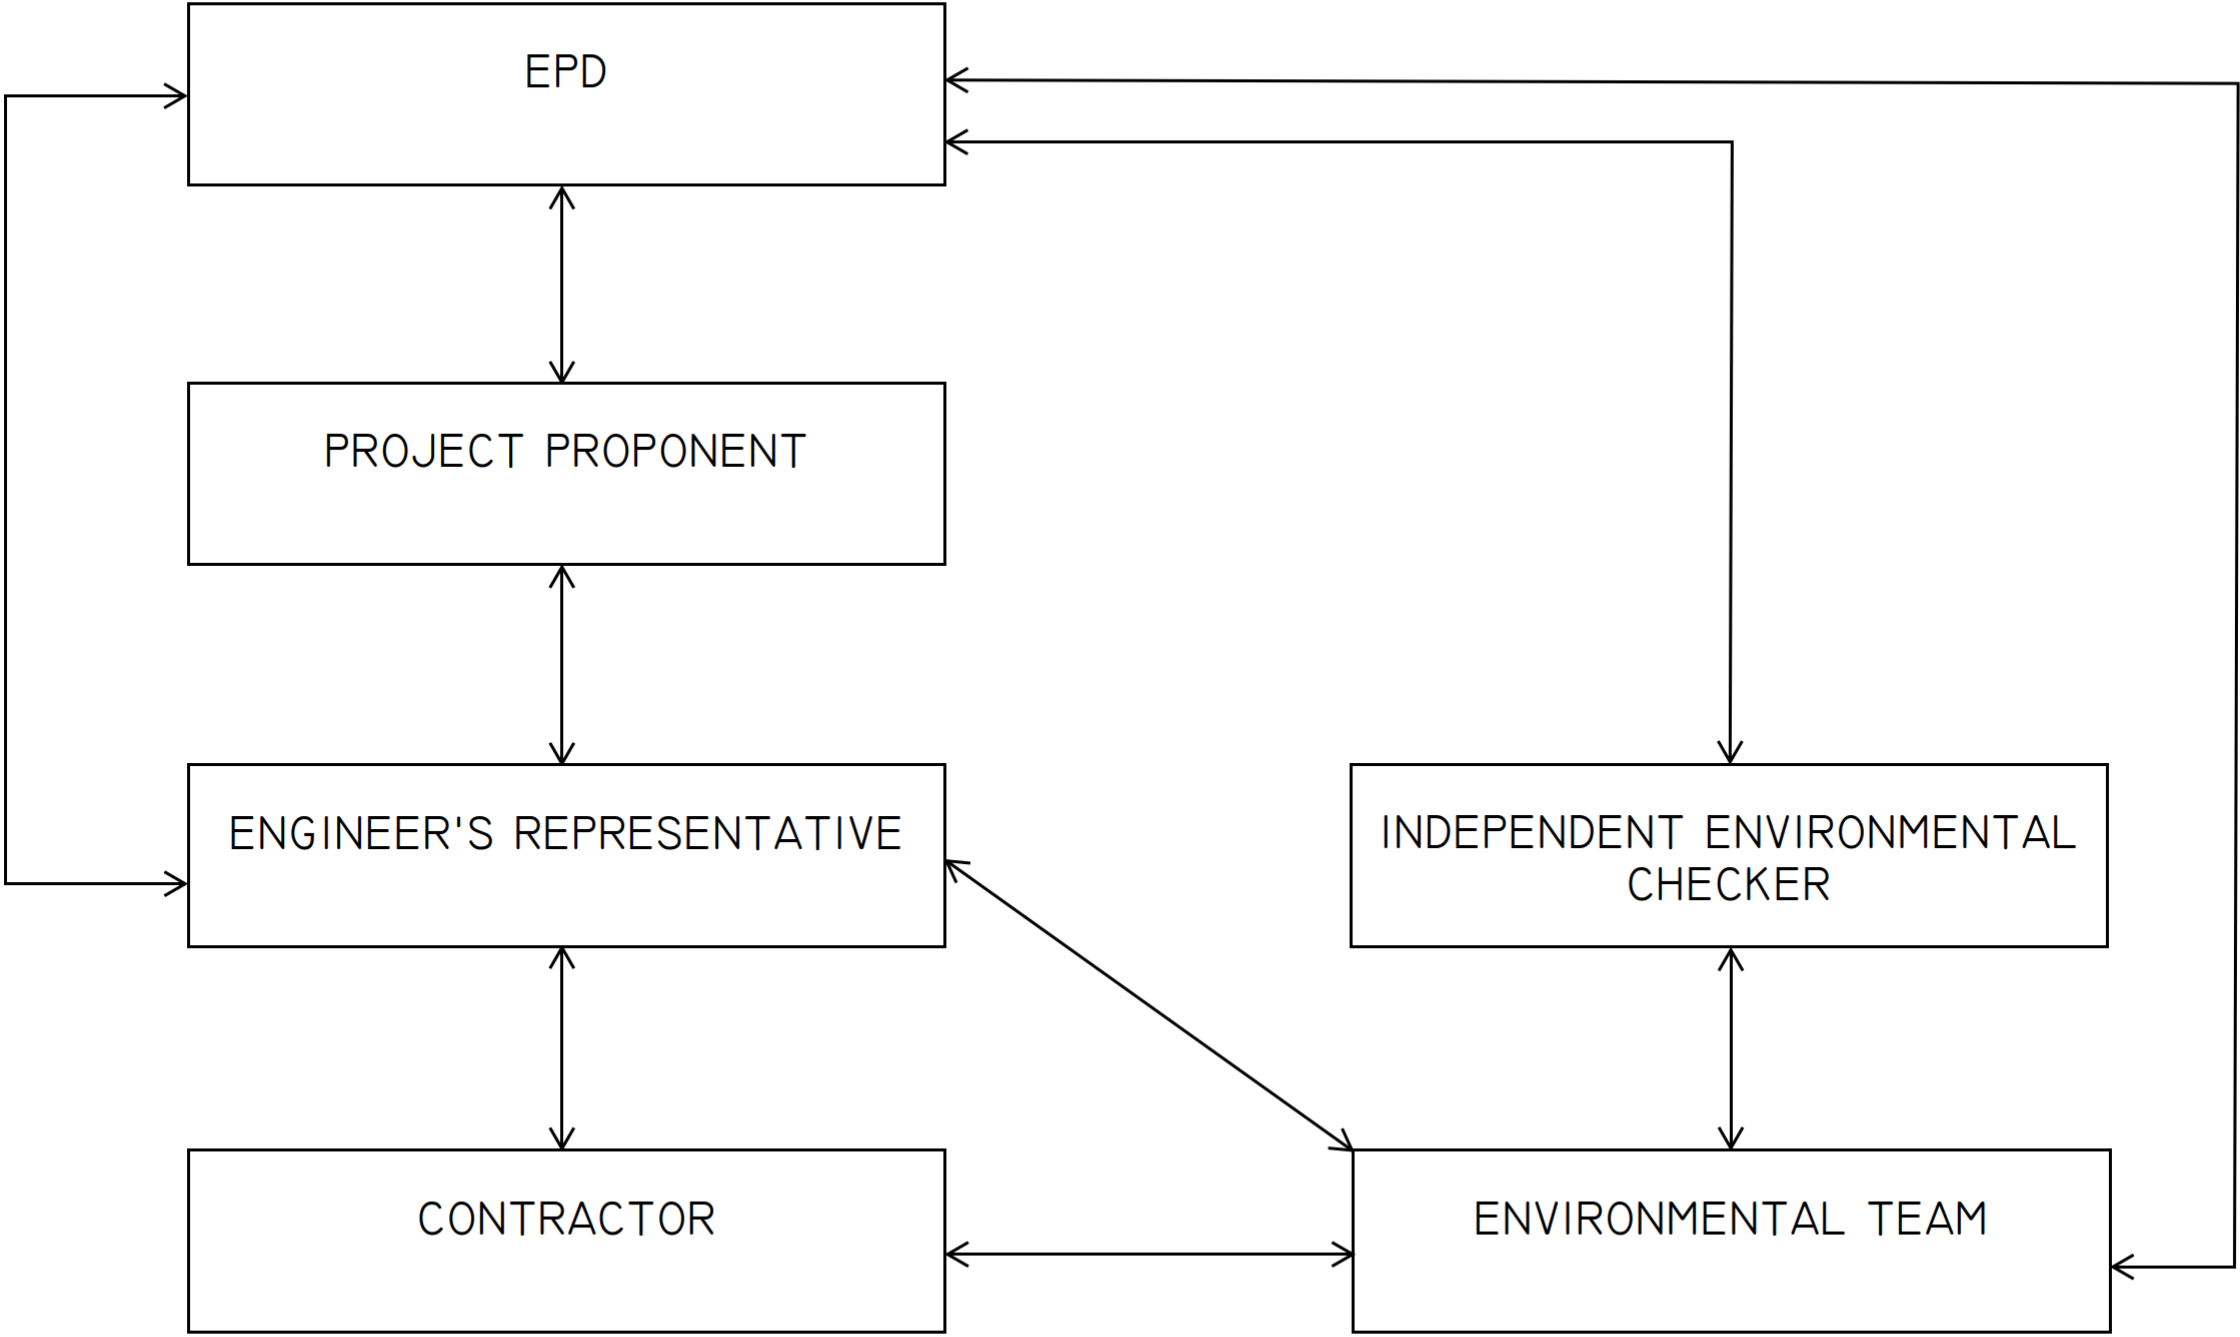

LEGEND:


↔ LINE OF COMMUNICATION

AECOM

PROJECT
项目

TOLO HARBOUR
SEWERAGE OF
UNSEWERED AREAS
STAGE 2 -
INVESTIGATION, DESIGN
AND CONSTRUCTION

CLIENT
業主

渠務署
Drainage Services Department

CONSULTANT
工程顧問公司

AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS
分判工程顧問公司

ISSUE/REVISION
修訂

I/R 修訂	DATE 日期	DESCRIPTION 內容摘要	CHK. 校核

STATUS
階段

SCALE
比例

A1 1 : AS SHOWN

DIMENSION UNIT
尺寸單位

METRES

KEY PLAN
索引圖

PROJECT NO.
項目編號

60547289

CONTRACT NO.
合約編號

SHEET TITLE
圖紙名稱

PROJECT ORGANISATION

SHEET NUMBER
圖紙編號

60547289/EM&A/FIGURE 1.2

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

Appendix B

Construction Programme

	Activity	Days	Start	Finish	2023																2024				
					October					November					December					January					
					01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28			
Master Programme Rev.1 Updated to 31-Oct 23																									
Contractual Dates																									
Completion Date (Programmed)																									
KD1020	Section 2 - Completion of Tseng Tau Road and Associated Works	0		30-Dec-23*																					
KD1030	Section 3 - Completion of TBM Works and Associated Works outside Green Area	0		31-Oct-23*																					
Keydates (Target)																									
KDT08	KD8 - Completion of Watermain outside Green Area	0		31-Oct-23*																					
KDT09	KD9 - Completion of Rising Main outside Green Area	0		31-Oct-23*																					
KDT10	KD10 - Completion of Sai Sha Road Westbound	0		31-Dec-23*																					
KDT11A	KD11A - Completion of Nai Chung & Kwun Hang Footbridge	0		31-Oct-23*																					
KDT11B	KD11B - Completion of Ma Kwu Lam Footbridge	0		31-Dec-23*																					
KDT13A	KD13A - Completion of all UU connections for Site C OP and Tseng Tau Road	0		31-Oct-23*																					
KDT13B	KD13B - Completion of all works for Sit B OP (except Sai O Pumping Station)	0		31-Oct-23*																					
KDT15	KD15 - Completion of all TBM Works (excluding Rising Mains and Gas Main Installation ar	0		31-Oct-23*																					
Keydates (Programmed)																									
KD08	KD8 - Completion of Watermain outside Green Area	0		31-Oct-23*																					
KD09	KD9 - Completion of Rising Main outside Green Area	0		31-Oct-23*																					
KD11A	KD11A - Completion of Nai Chung & Kwun Hang Footbridge	0		29-Dec-23*																					
KD11B	KD11B - Completion of Ma Kwu Lam Footbridge	0		30-Dec-23*																					
KD13A	KD13A - Completion of all UU connections for Site C OP and Tseng Tau Road	0		30-Dec-23*																					
KD13B	KD13B - Completion of all works for Sit B OP (except Sai O Pumping Station)	0		27-Nov-23*																					
KD15	KD15 - Completion of all TBM Works (excluding Rising Mains and Gas Main Installation ar	0		31-Oct-23*																					
Sai Sha Road & Associated Works (Section 1 of the Works)																									
Public Transport Interchange and Public Car Park at Sai O																									
Public Car Park and Public Mini Bus Terminus																									
PCP2180	E&M, ABWF and Misc. for New Toilet and Refuse Collection Point	130	12-Oct-23 A	19-Mar-24																					
PCP2250	Roadworks	169	23-Oct-21 A	15-Nov-23																					
Remaining Works at New PTI																									
PCP2260	Relocation of temporary car park at new PTI to permanent car park	7	30-Nov-23	07-Dec-23																					
PCP2270	Construct permanent kerb line, bus shelter, meters, and road surface for Bus Terminus	78	07-Dec-23	13-Mar-24																					
Nai Chung Footbridge FB1																									
ABWF, E&M Installation																									
NCFB3010	E&M Works at Eastbound	27	31-Aug-23 A	17-Nov-23																					
NCFB3030	E&M Works at Westbound	45	24-Aug-23 A	17-Nov-23																					
NCFB3045	Cable containment and final cabling	21	07-Nov-23	30-Nov-23																					
NCFB3050	E&M Works T&C	28	14-Nov-23	15-Dec-23																					
NCFB3060	Lift - EMSD Inspection and issue permit	29	22-Nov-23	27-Dec-23																					
NCFB3110	ABWF Works	180	15-Nov-22 A	30-Nov-23																					
Kwun Hang Footbridge FB2																									
Eastbound																									
KHFB1080	Temporary TTM to new W/B and Remove the Portal Frames at E/B	12	17-Oct-23 A	28-Oct-23 A																					
ABWF, E&M Installation																									
KHFB3010	E&M Works at Eastbound	58	24-Jul-23 A	17-Nov-23																					
KHFB3030	E&M Works at Westbound	25	29-Jul-23 A	17-Nov-23																					
KHFB3045	Cable containment and final cabling	16	13-Nov-23	30-Nov-23																					
KHFB3050	E&M Works T&C	22	21-Nov-23	15-Dec-23																					
KHFB3060	Lift - EMSD Inspection and issue permit	36	16-Nov-23	29-Dec-23																					
KHFB4010	ABWF Works	180	25-Oct-22 A	30-Nov-23																					
Ma Kwu Lam Footbridge FB3																									
Eastbound																									
Stage 3 Reinstatement Works																									
MKLFB2210	Remove the Portal Frame at TTR W/B incl. concrete blocks at median supports	6	04-Oct-23 A	10-Oct-23 A																					
MKLFB2230	TTM for Divert Traffic to TTR W/B	1	04-Nov-23	04-Nov-23																					
MKLFB2240	Remove the Portal Frame at TTR E/B incl. concrete blocks at median supports	6	06-Nov-23	11-Nov-23																					
MKLFB2250	Complete Permanent Kerb Line, Roadwork and Resurfacing at TTR E/B	30	06-Nov-23	09-Dec-23																					
MKLFB2260	TTM to Divert One Lane from TTR W/B to E/B	1	10-Dec-23	10-Dec-23																					
MKLFB2270	Complete Permanent Kerb Line and Roadwork at TTR W/B	16	11-Dec-23	30-Dec-23																					
MKLFB2280	Complete Remaining Footpath and Planter	16	20-Dec-23	10-Jan-24																					
ABWF, E&M Installation																									
MKLFB4010	E&M Works at Eastbound	49	17-Aug-23 A	05-Dec-23																					
MKLFB4030	E&M Works at Westbound	75	17-Aug-23 A	05-Dec-23																					
MKLFB4041	Lift - MKL1 (2 nrs)	50	31-Aug-23 A	15-Dec-23																					
MKLFB4042	Lift - MKL4 (2 nrs)	50	31-Aug-23 A	15-Dec-23																					

	Activity	Days	Start	Finish	2023												2024					
					01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28
	MKLFB4045	Cable containment and final cabling	6	16-Oct-23 A	06-Nov-23																	
	MKLFB4050	E&M Works T&C	34	07-Nov-23	15-Dec-23																	
	MKLFB4060	Lift - EMSD Inspection and issue permit	37	16-Nov-23	30-Dec-23																	
	MKLFB5010	ABWF Works	228	11-Mar-23 A	30-Dec-23																	
Area 1 - Sai Sha Road (R100: Ch100-280)																						
West Bound																						
	SSR1550	Drainage (carrier), 176m	35	01-Aug-23 A	28-Oct-23 A																	
	SSR1570	Site formation work	25	25-Sep-23 A	03-Nov-23																	
	SSR1590	Noise barrier steelwork, 169m, 5m/Day	20	31-Oct-23	22-Nov-23																	
	SSR1600	Roadworks	24	02-Oct-23 A	15-Nov-23																	
Utilities Works																						
	SSR1580	CLP (2 x 180m), 50m/wk	36	14-Aug-23 A	13-Nov-23																	
	SSR1585	CMHK-180m,HGC-180m,HKBN-180m,HKT-180m,SMT-180m	36	18-Sep-23 A	20-Nov-23																	
Soft Landscaping Works																						
	SSR1810	Soft Lanscaping Works	42	21-Nov-23	11-Jan-24																	
Area 2 - Sai Sha Road (R100: Ch280-450)																						
West Bound																						
	SSR2620	Noise barrier steelwork, 196m	24	25-May-23 A	15-Nov-23																	
Utilities Works																						
	SSR2610	CLP (2 x 170m), 50m/wk	24	24-Jul-23 A	13-Nov-23																	
	SSR2640	CATV-25m,CMHK-170m,HGC-170m,HKBN-80m,HKT-170m,SMT-170m	24	16-Oct-23 A	20-Nov-23																	
Soft Landscaping Works																						
	SSR2810	Soft Lanscaping Works	48	07-Nov-23	04-Jan-24																	
Area 3 - Sai Sha Road (R100: Ch450-800)																						
West Bound																						
	SSR3560	Drainage (carrier), stage 2 - 146m	52	29-May-23 A	03-Nov-23																	
	SSR3575	Site formation work - stage 2	12	23-Oct-23 A	06-Nov-23																	
	SSR3590	Noise barrier steelwork, 360m	18	31-Oct-23	20-Nov-23																	
	SSR3600	Roadworks	24	25-Oct-23 A	16-Nov-23																	
Utilities Works																						
	SSR3580	CLP (350m), 50m/wk	18	16-Oct-23 A	13-Nov-23																	
	SSR3610	CMHK-350m,HGC-350m,HKBN-60m,HKT-350m,SMT-350m, 2WF	18	31-Oct-23	20-Nov-23																	
Slope No.8																						
	SSR3790	Construct U Channels & Hydroseeding	70	06-Mar-23 A	14-Oct-23 A																	
Soft Landscaping Works																						
	SSR3810	Soft Lanscaping Works	56	31-Oct-23	06-Jan-24																	
Areas 4 - Sai Sha Road (R100: Ch800-960)																						
West Bound																						
	SSR4578	Site formation work	24	28-Aug-23 A	06-Nov-23																	
	SSR4590	Noise barrier steelwork, 153m	24	23-Oct-23 A	27-Nov-23																	
	SSR4595	Roadworks for TTM to remove of KHFB eastbound portal	24	16-Sep-23 A	16-Nov-23																	
Utilities Works																						
	SSR4700	Waterworks (DN400/DN600, 190m incl W/B)	78	07-Jan-22 A	10-Nov-23																	
	SSR4710	CLP (310m), 50m/wk	24	23-Oct-23 A	20-Nov-23																	
	SSR4720	CATV-30m,CMHK-310m,HGC-310m,HKBN-30m,HKT-310m,SMT-310m)	24	31-Oct-23	27-Nov-23																	
Soft Landscaping Works																						
	SSR4810	Soft Lanscaping Works	32	28-Nov-23	06-Jan-24																	
Che Ha Road																						
Section 1 - Che Ha Road Roundabout																						
	CHR0180	Sewerage and drainage works	39	07-Aug-23 A	30-Sep-23 A																	
	CHR0190	Waterworks and utilities	24	31-Oct-23	27-Nov-23																	
	CHR0200	Formation	18	14-Sep-23 A	03-Nov-23																	
	CHR0210	Roadworks	24	18-Sep-23 A	24-Nov-23																	
	CHR0220	Footpath	36	28-Nov-23	11-Jan-24																	
	CHR0230	Soft landscaping works	12	12-Jan-24	25-Jan-24																	
	CHR0240	Implement TTM from Sai Sha Road to Che Ha Village via new roundabout	3	25-Nov-23	28-Nov-23																	
Section 2 - Che Ha Road Roundabout to Village Junction																						
	CHR0320	Sewerage and drainage works	50	19-May-23 A	20-Nov-23																	
	CHR0330	Waterworks and utilities	34	13-Nov-23	21-Dec-23																	
	CHR0340	Formation	18	23-Oct-23 A	13-Nov-23																	
	CHR0350	Roadworks	24	27-Oct-23 A	27-Nov-23																	
	CHR0360	Footpath	28	22-Dec-23	26-Jan-24																	
Section 3 - Village Junction to End of Che Ha Road																						
	CHR0520	Settle village issue	0	31-Oct-23*																		

	Activity	Days	Start	Finish	2023												2024						
					October				November				December				January						
					01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	
CHR0530	Sewerage and drainage works	96	31-Oct-23	24-Feb-24																			
Section 4 - Remaining Works at Junction																							
CHR0580	Sewerage and drainage works	24	29-Nov-23	28-Dec-23																			
CHR0590	Waterworks and utilities	24	29-Dec-23	26-Jan-24																			
CHR0600	Formation	18	27-Jan-24	20-Feb-24																			
Areas 5 - Sai Sha Road (R100: Ch960-1110)																							
West Bound																							
SSR5550	Drainage (carrier), 150m	58	08-May-23 A	11-Nov-23																			
SSR5560	Site formation work	18	21-Oct-23 A	14-Nov-23																			
SSR5570	Noise barrier steelwork, 98m	18	08-Nov-23	28-Nov-23																			
SSR5580	Roadworks	24	26-Oct-23 A	17-Nov-23																			
Utilities Works																							
SSR5700	Waterworks (DN400/DN600, 150m incl W/B)	75	11-Jan-23 A	09-Nov-23																			
SSR5710	CLP (310m), 50m/wk	24	13-Nov-23	09-Dec-23																			
SSR5720	CATV-30m,CMHK-310m,HGC-310m,HKBN-30m,HKT-310m,SMT-310m)	24	13-Nov-23	09-Dec-23																			
Soft Landscaping Works																							
SSR5810	Soft Lanscaping Works	32	11-Dec-23	19-Jan-24																			
Area 6 - Sai Sha Road (R100: Ch1100 - R200: Ch180)																							
West Bound (Stage 2)																							
SSR6585	Tree Transplant to Roundabout	18	31-Oct-23	20-Nov-23																			
SSR6610	Roadworks (incl Permanent Roundabout & Fire Hydrants)	90	07-Oct-22 A	14-Oct-23 A																			
Soft Landscaping Works																							
SSR6810	Soft Lanscaping Works	56	11-Sep-23 A	20-Nov-23																			
Area 7 - Sai Sha Road (R200: Ch180 - R300: Ch140)																							
West Bound																							
SSR7620	Site formation work	36	21-Jul-23 A	21-Oct-23 A																			
SSR7650	Roadworks	36	28-Jul-23 A	10-Nov-23																			
SSR7670	Implement roundabout at J/O of Sai Sha Road and Tseng Tau Road	1	27-Nov-23	27-Nov-23																			
Utilities Works																							
SSR7630	CLP (140m), 50m/wk	24	21-Jul-23 A	14-Oct-23 A																			
SSR7640	CATV-140m,CMHK-140m,HGC-140m,HKBN-140m,HKT-140m,SMT-140m,VTL-140m)	24	16-Oct-23 A	25-Oct-23 A																			
SSR7660	Completion of Area 7	0		27-Nov-23*																			
Soft Landscaping Works																							
SSR7810	Soft Lanscaping Works	24	31-Oct-23	27-Nov-23																			
Area 8 - Sai Sha Road (R300: Ch140-314)																							
East Bound																							
SSR8060	Installation of Noise Barrier Panels at NB17/18	30	31-Oct-23*	04-Dec-23																			
West Bound																							
SSR8525	Stage 1 - Drainage (carrier)	108	14-Feb-23 A	21-Oct-23 A																			
SSR8540	Stage 1 - Site formation work	12	28-Sep-23 A	24-Oct-23 A																			
SSR8560	Stage 1 - Roadworks	12	16-Oct-23 A	28-Oct-23 A																			
SSR8580	Implement at J/O SSR and T in Liu Road for remaining DN900 drain	1	29-Oct-23 A	29-Oct-23 A																			
SSR9100	Stage 2 - Drainage (remaining DN900 drain)	18	30-Oct-23 A	20-Nov-23																			
SSR9110	Stage 2 - Site formation work	3	21-Nov-23	23-Nov-23																			
SSR9120	Stage 2 - Roadworks	3	24-Nov-23	27-Nov-23																			
Utilities Works																							
SSR8550	CLP (175m), 50m/wk	18	25-Sep-23 A	24-Oct-23 A																			
SSR8570	CMHK-175m,HGC-175m,SMT-175m	18	20-Oct-23 A	26-Oct-23 A																			
Soft Landscaping Works																							
SSR8810	Soft Lanscaping Works	26	28-Nov-23	29-Dec-23																			
Resurfacing for E/B Sai Sha Road Area 1 - 6																							
SSR9050	Completion of SSR Westbound Area 1 - 6	0		28-Nov-23																			
SSR9060	Implement TTA for Diversion of 1 traffic lane to SSR Westbound Area 1 - 6	3	29-Nov-23	01-Dec-23																			
SSR9065	Construct outstanding kerbs and planter at SSR Eastbound Fast Lane Area 1 - 6	18	02-Dec-23	22-Dec-23																			
SSR9070	Resurfacing for SSR Eastbound Fast Lane Area 1 - 6	18	09-Dec-23	02-Jan-24																			
SSR9080	Implement TTA for Diversion of 1 traffic lane to SSR Eastbound Fast Lane Area 1 - 6	3	03-Jan-24	05-Jan-24																			
SSR9085	Construct outstanding kerbs and planter at SSR Eastbound Fast Lane Area 1 - 6	18	06-Jan-24	26-Jan-24																			
SSR9090	Resurfacing for SSR Eastbound Slow Lane Area 1 - 6	18	13-Jan-24	02-Feb-24																			
Resurfacing for E/B Sai Sha Road Area 6 - 8																							
SSR9010	Completion of SSR Westbound Area 6 - 8	0		27-Nov-23																			
SSR9015	Implement TTA for Diversion of 1 traffic lane to SSR Westbound Area 6 - 8	2	28-Nov-23	29-Nov-23																			
SSR9017	Construct outstanding kerbs and planter at SSR Eastbound Fast Lane Area 6 - 8	14	30-Nov-23	15-Dec-23																			
SSR9020	Resurfacing for SSR Eastbound Fast Lane Area 6 - 8	14	07-Dec-23	22-Dec-23																			
SSR9025	Implement TTA for Diversion of 1 traffic lane to SSR Eastbound Fast Lane Area 6 - 8	2	23-Dec-23	27-Dec-23																			

	Activity	Days	Start	Finish	2023												2024						
					October				November				December				January						
					01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	ay
	SSR9027	Construct outstanding kerbs and planter at SSR Eastbound Fast Lane Area 6 - 8	14	28-Dec-23	13-Jan-24																		
	SSR9028	Resurfacing for SSR Eastbound Slow Lane Area 6 - 8	14	05-Jan-24	20-Jan-24																		
Utilities Connection																							
CLP																							
	UC1010	Completion of CLP Works	0		23-Dec-23																		
	UC1015	CLP Connection	40	27-Dec-23	14-Feb-24*																		
Towngas																							
	UC1020	Completion of Towngas Works	0		31-Oct-23																		
	UC1030	Towngas Connection Works (say, 2 months)	59	31-Oct-23	11-Jan-24*																		
Telecommunication																							
	UC1040	Completion of Telecommunication Ducting	0		28-Dec-23																		
	UC1050	Wiring and Connection for Telecommunication Companies	26	29-Dec-23	30-Jan-24*																		
Waterworks																							
	UC1060	Completion of Waterworks (Outside Green Area)	0		31-Oct-23																		
	UC1070	Completion of Waterworks (Green Area) except Area 7 to Tin Liu Road	0		10-Nov-23																		
	UC1080	Waterwork Connection	52	11-Nov-23	13-Jan-24*																		
Area 7.1 - Access Road to Tin Liu Village																							
Stage 2a - Soldier Pile Wall SPW3 Zone 1																							
	TLR2520	Construct additional cantilever beam for soldier pile wall at dry season	48	01-Nov-23*	28-Dec-23																		
Stage 3 - Roadworks																							
	TLR3134	Zone 1: remaining drainage	24	16-Sep-23 A	13-Nov-23																		
	TLR3136	Zone 1: CLP cables	12	14-Nov-23	27-Nov-23																		
	TLR3138	Zone 1: Roadworks (permanent 2nd half)	24	28-Nov-23	27-Dec-23																		
	TLR3140	Zone 1: Diversion to Permanent Road	6	28-Dec-23	04-Jan-24																		
	TLR3150	Zone 1: Remove Temp. Road and Reinstate Area	24	05-Jan-24	01-Feb-24																		
	TLR3210	Zone 2: Drainage, 50m	52	31-Oct-23	02-Jan-24																		
	TLR3225	Zone 2: gasmain and telecom duct	24	03-Jan-24	30-Jan-24																		
Tseng Tau Road (Section 2 of the Works)																							
Area 7.2 - Tseng Tau Road (R400: Ch100-250)																							
West bound																							
	TTR1527	Rising main from Site B (9 ways) (Nga Yiu Tau Road - RW6 Bay 10)	130	20-Oct-22 A	04-Oct-23 A																		
	TTR1535	Rising main from Site B (9 ways) (RW6 Bay 9 - RW 27-29)	48	17-Jul-23 A	09-Oct-23 A																		
	TTR1540	Drainage (carrier), 135m	68	28-Jun-23 A	30-Oct-23 A																		
	TTR1550	Drainage and surface channel behind RW6 and RW27-29	96	31-Oct-23 A	26-Feb-24																		
	TTR1560	Site formation work	36	22-Sep-23 A	31-Oct-23 A																		
	TTR1580	Noise barrier steelwork, 2WF	24	14-Oct-23 A	20-Nov-23																		
	TTR1590	Roadworks	36	28-Sep-23 A	03-Nov-23																		
Utilities Works																							
	TTR1570	CLP (2 x 150m), 50m/wk	26	09-Oct-23 A	23-Dec-23																		
	TTR2710	CMHK-60m,HGC-150m,HKBN-150m,HKT-230m,SMT-150m,TGT-30m,VTL-150m	26	16-Oct-23 A	28-Dec-23																		
Soft Landscaping Works																							
	TTR3010	Soft Lanscaping Works	24	29-Dec-23	26-Jan-24																		
Area 7.3 - Outstanding Works at Tseng Tau Road																							
Stage 3 - Footpath/Planter (Site B Side)																							
	A1775	Cable & lighting installation (by others)	26	25-Jul-23 A	20-Nov-23																		
Stage 4 - Soft Landscaping Works																							
	A1870	Completion of Outstanding Works at Tseng Tau Road	0		20-Nov-23																		
Tseng Tau Pumping Station																							
External Works and ABWF/E&M Works																							
	TTSPS1120	E&M works	140	21-Nov-22 A	20-Nov-23																		
	TTSPS1130	ABWF works (interior finish and building envelope)	100	25-Aug-22 A	20-Nov-23																		
	TTSPS1135	External works (fencing, planter, EVA, signage, etc)	26	03-May-23 A	20-Nov-23																		
T&C and Statutory Inspection																							
	TTSPS1140	T&C	23	25-Sep-23 A	15-Dec-23																		
	TTSPS1150	FSD Inspection, ASD Inspection, OP (after power on in mid Nov 2023)	9	19-Dec-23*	30-Dec-23																		
	TTSPS1160	Completion of Section 2	0		30-Dec-23*																		
Works Outside Green Area (Section 3 of the Works)																							
Waterworks Outside Green Area with 4 WF (Refer to Detailed Prog)																							
	WW1145	Testing of Waterworks from Work Front 1 to Work Front 4	53	30-Jun-23 A	01-Dec-23																		
Sai O Pumping Station (Section 4)																							
ABWF Works																							
	SOPS5010	Interior finish - pump room	52	25-Aug-23 A	02-Nov-23																		
	SOPS5020	Exterior finish	52	04-Sep-23 A	06-Nov-23																		

ID	Activity	Days	Start	Finish	2023												2024							
					October					November				December			2024							
					01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	any	
	SOPS5030	Roof finish	52	29-Sep-23 A	20-Nov-23																			
	SOPS5040	External works	40	07-Oct-23 A	16-Dec-23																			
	E&M Works and OP																							
	SOPS6010	CLP works - transformer room	101	31-Jul-23 A	30-Nov-23																			
	SOPS6020	E&M works - pump room below ground	71	09-Oct-23 A	03-Jan-24																			
	SOPS6030	E&M works - pump room above ground	82	09-Oct-23 A	16-Jan-24																			
	SOPS6040	E&M works - external	64	17-Nov-23	02-Feb-24																			
	SOPS6060	Testing and Commissioning	48	02-Jan-24	29-Feb-24																			

Appendix C

Equipment Calibration Certificates

Air Quality Monitoring Equipment

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Model: Tisch TE-5170		Date of Calibration: 28-Sep-23	
Equipment No.: HVS-05		Next Calibration Date: 27-Nov-23	
Location:		Technician: Ho Woo	

CONDITIONS			
Sea Level Pressure (hPa):	1011.60	Corrected Pressure (mm Hg):	759
Temperature (°C):	30.3	Temperature (K):	303

CALIBRATION ORIFICE			
Model: Tisch TE-5025A	Qstd Slope: 2.08482		
Serial No.: 2456	Qstd Intercept: -0.02977		
Calibration Date: 1-Jun-23	Expiry Date: 1-Jun-24		

CALIBRATIONS							
Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m³/min)	I (chart)	IC (corrected)	LINEAR REGRESSION
18	6.20	-7.20	13.400	1.753	57.00	56.45	Slope = 22.3792 Intercept = 16.3483 Corr. coeff.= 0.9943
13	4.90	-6.00	10.900	1.583	51.00	50.51	
10	3.40	-4.20	7.600	1.324	47.00	46.55	
7	2.20	-3.50	5.700	1.148	42.00	41.60	
5	1.20	-1.90	3.100	0.851	36.00	35.66	

Calculations:


Qstd = 1/m[Sqrt(H2O(Pa/Pstd)(Tstd/Ta))-b]
IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate
IC = corrected chart response
I = actual chart response
m = calibrator Qstd slope
b = calibrator Qstd intercept
Ta = actual temperature during calibration (deg K)
Pa = actual pressure during calibration (mm Hg)
Tstd = 298 deg K
Pstd = 760 mm Hg

For subsequent calculation of sampler flow:
1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

m = sampler slope
b = sampler intercept
I = chart response
Tav = daily average temperature
Pav = daily average pressure

FLOW RATE CHART

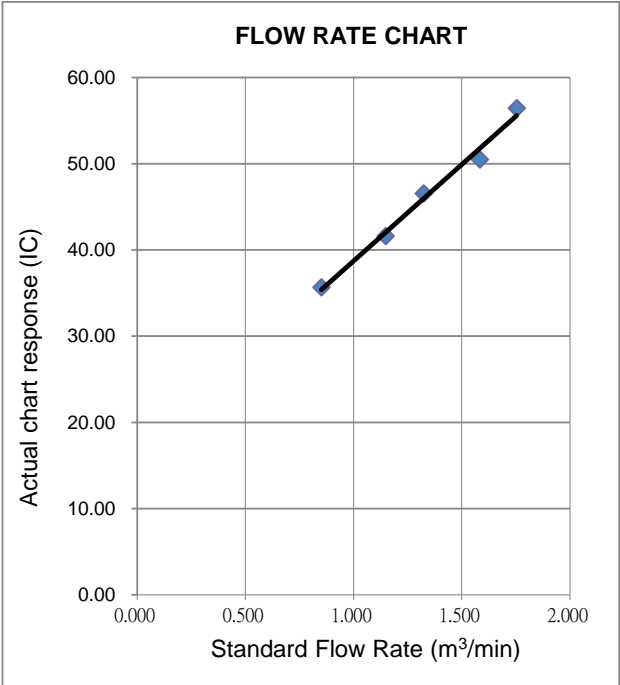

Calibrated by : h/oo Date : 28 Sep 2023 Supervised by : [Signature] Date : 28 Sep 2023

Certificate of Calibration

Calibration Certification Information

Cal. Date: June 1, 2023 Rootsmer S/N: 438320 Ta: 295 °K
Operator: Jim Tisch Pa: 751.8 mm Hg
Calibration Model #: TE-5025A Calibrator S/N: 2456

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4360	3.2	2.00
2	3	4	1	1.0210	6.4	4.00
3	5	6	1	0.9080	8.0	5.00
4	7	8	1	0.8670	8.8	5.50
5	9	10	1	0.7170	12.8	8.00

Data Tabulation

Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
0.9951	0.6929	1.4137	0.9957	0.6934	0.8859
0.9908	0.9704	1.9993	0.9915	0.9711	1.2528
0.9887	1.0889	2.2353	0.9894	1.0896	1.4007
0.9876	1.1391	2.3444	0.9883	1.1399	1.4690
0.9823	1.3700	2.8275	0.9830	1.3710	1.7717
QSTD	m=	2.08482	QA	m=	1.30548
	b=	-0.02977		b=	-0.01866
	r=	0.99997		r=	0.99997

Calculations

Vstd=	$\Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta)$	Va=	$\Delta Vol((Pa-\Delta P)/Pa)$
Qstd=	Vstd/ΔTime	Qa=	Va/ΔTime
For subsequent flow rate calculations:			
Qstd=	$1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa=	$1/m \left(\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions

Tstd: 298.15 °K

Pstd: 760 mm Hg

Key

ΔH: calibrator manometer reading (in H2O)

ΔP: rootsmer manometer reading (mm Hg)

Ta: actual absolute temperature (°K)

Pa: actual barometric pressure (mm Hg)

b: intercept

m: slope

RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

CALIBRATION REPORT OF WIND METER


EP No.: EP-597/2021		Date of Calibration:	29-May-2023
Location:	Sai O Trunk Sewer Sewage Pumping Station	Next Calibration Date:	28-Nov-2023
Brand:	Global Water	Technician:	Ho Woo
Model:	GL500-7-2	Equipment ID:	WS-03
Anemometer			
Brand:	Smart Sensor	Equipment ID:	WS-03
Model:	AR816		
Procedures:			
1. Wind Still Test:	The wind speed sensor was held by hand until stabilized.		
2. Wind Speed Test:	By direct comparison the reading between the wind speed sensor and the Anemometer.		
3. Wind Direction Test:	The wind meter was calibrated in-situ and compared with a marine compass from four directions.		

Wind Still Test:

Wind Speed (m/s)
0.00

Wind Speed Test:

Global Water (m/s)	Anemometer (m/s)
1.0	1.3
2.2	2.6
3.1	3.4

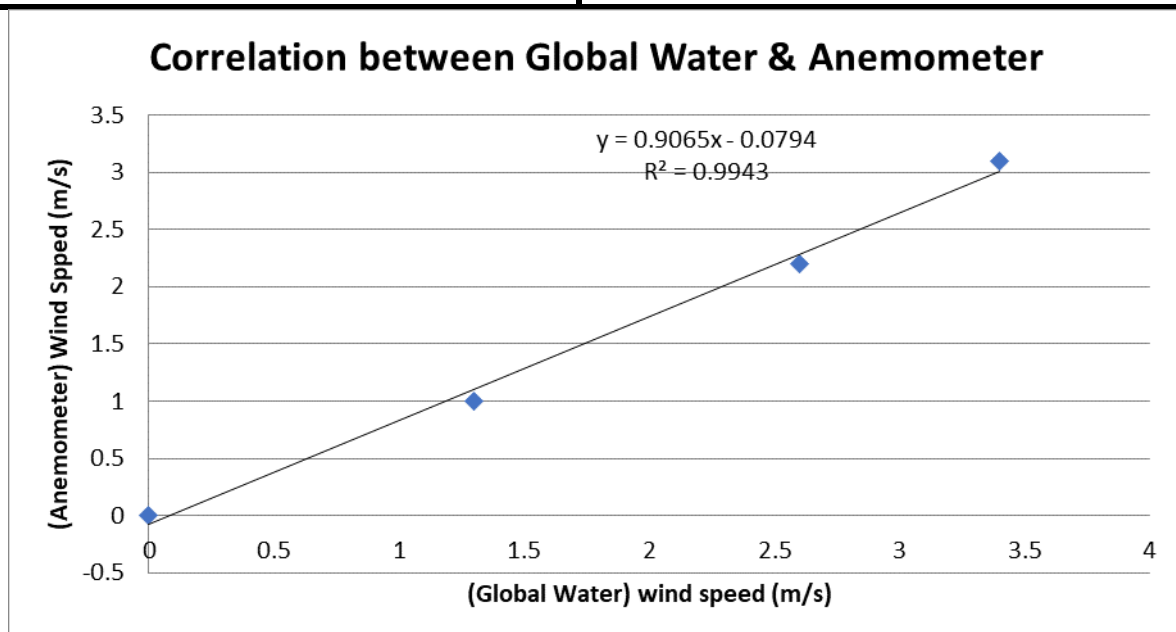

Remarks:

- Actual Wind Speed Value (m/s) = $0.9065 \times (\text{Reading of Global Water Instrument}) + 0.0794$
- Correlation coefficient (R^2) = 0.9943
- Acceptable Range: $R^2 \geq 0.99$



FUGRO TECHNICAL SERVICES LIMITED

Room 723 & 725, 7/F, Block B,
Profit Industrial Building,
1-15 Kwai Fung Crescent, Kwai Fong,
Hong Kong.

CALIBRATION REPORT OF WIND METER

Wind Direction Test:

	Marine Compass (o)
0	2
53	54
91	94
271	273

Shum Tung
Project Consultant

Report Date: 29/05/2023

Report No. : 212769CA233072

Page 1 of 1

CALIBRATION CERTIFICATE OF ANEMOMETER**Client Supplied Information**

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Details of Unit Under Test, UUT

Description : Anemometer

Manufacturer : Smart Sensor

Model No. : AR816

Serial No. : NA

Equipment ID.: AM-001

Next Calibration Date : 23-Apr-2024

Laboratory Information

Details of Reference Equipment –

Description : Reference Anemometer

Equipment ID.: R-101-4

Date of Calibration : 24-Apr-2023 Ambient Temperature : 22 °C

Calibration Location : Calibration Laboratory of FTS

Method Used : In-house method R-C-279

Calibration Results :

Reference Reading (m/s)	UUT Reading (m/s)	Error (m/s)
2.00	2.0	0.0
4.00	4.0	0.0
6.00	6.0	0.0
8.00	8.2	0.2
10.02	10.3	0.3

Remark :

1. The equipment being used in this calibration is traceable to recognized National Standards.
2. The reported readings in this calibration are an average from 10 trials.

Checked by :  Date : 27-4-2023 Certified by : KT Leung Date : 27-4-2023
CA-R-297 (22/07/2009) Leung Kwok Tai (Assistant Manager)

**** End of Report ****

Noise Monitoring Equipment

Report no.: 212769CA222607

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND LEVEL METER

Client Supplied Information

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Details of Unit Under Test, UUT -

Description : Sound Level Meter

Manufacturer : Casella

Model No. :

Serial No. :

Equipment ID :

Next Calibration Date :

Specification Limit :

Meter	Microphone	Preamplifier
CEL-63X	CE-251	CEL-495
1488269	03914	003984

N/A

06-Nov-2023

EN 61672-1: 2003 Class 1

Laboratory Information

Details of Reference Equipment -

Description : B & K Acoustic Multifunction Calibrator 4226 (Traditional free field setting)

Equipment ID. : R-108-1

Date of Receipt : 03-Nov-2022

Date of Calibration : 07-Nov-2022

Calibration Location : Calibration Laboratory of FTS

Ambient Temperature : 20±2 °C

Method Used : By direct comparison


Relative Humidity : <80% R.H.

Calibration Results :


Parameters		Mean Value (dB)	Specification Limit(dB)
A-weighting frequency response	4000Hz	1.0	2.6 to -0.6
	2000Hz	1.2	2.8 to -0.4
	1000Hz	-0.1	1.1 to -1.1
	500Hz	-3.4	-1.8 to -4.6
	250Hz	-8.8	-7.2 to -10.0
	125Hz	-16.2	-14.6 to -17.6
	63Hz	-26.3	-24.7 to -27.7
Differential level linearity	94dB-104dB	0.0	± 0.6
	104dB-114dB	0.0	± 0.6

Remarks :

- The equipment used in this calibration is traceable to recognized National Standards.
- The mean value is the average of four measurements.
- For calibration: Reference SPL are 94, 104 & 114dB, range setting is 20-140dB & time weighting is fast
- The UUT does comply with EN 61672-1: 2003 Class 1 sound level meter for the above measurement.
- The values given in this Calibration Certificate only relate to unit under test and the values measured at the time of the test. Any uncertainties will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling or the capability of any other laboratory to repeat the measurement.

Checked by : 
CA-R-297 (22/07/2009)

Date : 10-11-2022

Certified by : 
Leung Kwok Tai (Assistant Manager)

Date : 10-11-2022

** End of Report **

Report no.: 212769CA223056(1)

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND LEVEL METER

Client Supplied Information

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Details of Unit Under Test, UUT -

Description : Sound Level Meter
Manufacturer : Casella

	Meter	Microphone	Preamplifier
Model No.	CEL-63X	CE-251	CEL-495
Serial No.	4181568	03133	003967

Equipment ID : N/A

Next Calibration Date : 03-Jan-2024

Specification Limit : EN 61672-1: 2003 Class 1

Next Calibration Date : 03-Jan-2024

Laboratory Information

Details of Reference Equipment -

Description : B & K Acoustic Multifunction Calibrator 4226 (Traditional free field setting)
Equipment ID. : R-108-1

Date of Receipt UUT : 30-Dec-2022

Date of Calibration : 04-Jan-2023

Calibration Location : Calibration Laboratory of FTS

Ambient Temperature : 20±2 °C

Method Used : By direct comparison

Relative Humidity : <80% R.H.

Calibration Results :

Parameters	Mean Value (dB)	Specification Limit(dB)
A-weighting frequency response	4000Hz	1.5
	2000Hz	1.4
	1000Hz	0.2
	500Hz	-3.3
	250Hz	-8.6
	125Hz	-16.0
	63Hz	-26.1
Differential level linearity	94dB-104dB	0.0
	104dB-114dB	0.0

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. For calibration: Reference SPL are 94, 104 & 114dB, range setting is 20-140dB & time weighting is fast
4. The UUT does comply with EN 61672-1: 2003 Class 1 sound level meter for the above measurement.
5. The values given in this Calibration Certificate only relate to unit under test and the values measured at the time of the test. Any uncertainties will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling or the capability of any other laboratory to repeat the measurement.

Checked by : SLH Date : 11-1-2023 Certified by : K.L. Leung Date : 11-1-2023

CA-R-297 (22/07/2009)

Leung Kwok Tai (Assistant Manager)

** End of Report **

10-80



**Certificate of
Conformance and Calibration for**

CEL-120 Acoustic Calibrator

Applicable Standards :- IEC 60942: 2003 & ANSI S1.40: 2006

CEL-120/1 Class 1 ☒

CEL-120/2 Class 2 ☐

Serial No: 2525896

Firmware: 04

Temperature: 22.9 °C Pressure: 1017 mb %RH 56

Frequency = 1.00kHz ± 2Hz T.H.D. = < 1%	Calibration Level
SPL @ 114.0dB Setting	<u>114.01</u> dB
SPL @ 94.0dB Setting (CEL-120/1 only)	<u>93.99</u> dB/N.A

Engineer: [Signature] Date: 03 NOV 2022

Company test equipment and acoustic working standards, used for conformance testing, are subject to periodic calibration, traceable to UK national standards, in accordance with the company's ISO9001 Quality System.

DECLARATION OF CONFORMITY

This certificate confirms that the instrument specified above has been produced and tested to comply with the manufacturer's published specifications and the relevant European Community CE directives.

Casella
Regent House, Wolsley Road, Kempston, Bedford. MK42 7JY
Phone: +44 (0) 1234 844100 Fax: +44 (0) 1234 841490
E-mail: info@casellasolutions.com
Web: www.casellasolutions.com

198032A-02

Report no.: 212769CA223056(2)

Page 1 of 1

CALIBRATION CERTIFICATE OF SOUND CALIBRATOR

Client Supplied Information

Client : Fugro Technical Services Ltd.

Project : Calibration Services

Details of Unit Under Test, UUT -

Description : Sound Calibrator
 Manufacturer : Casella (Model CEL-120/1)
 Serial No. : 4358250
 Equipment ID : N/A

Next Calibration Date : ---

Specification Limit : EN 60942: 2003 Class 1

Laboratory Information

Details of Calibration Equipment

Description : Reference Sound level meter
 Equipment ID. : R-119-2

Date of Receipt UUT : 30-Dec-2022

Date of Calibration : 04-Jan-2023

Calibration Location : Calibration Laboratory of FTS Ambient Temperature : 20±2 °C

Method Used : By direct comparison Relative Humidity : <80% R.H.

Calibration Results :

Parameters (Setting of UUT)	Mean Value (error of measurement)	Specification Limit(dB)
94dB	5.4 dB	±0.4dB
114dB	5.5 dB	

Remarks :

1. The equipment used in this calibration is traceable to recognized National Standards.
2. The mean value is the average of four measurements.
3. The equipment under test does not comply with the specification limit.
4. The values given in this Calibration Certificate only relate to the unit-under-test and the values measured at the time of the test. Any uncertainties quoted will not include allowances for the environmental changes, variation and shock during transportation, or the capability of any other laboratory to repeat the measurement.

Checked by : NS Date : 12-1-2023 Certified by : KI Leung Date : 12-1-2023
 CA-R-297 (22/07/2009)

Leung Kwok Tai (Assistant Manager)

**** End of Report ****

Appendix D

Environmental Monitoring Schedule

Project: EP-597/2021 Sai O Trunk Sewer Sewage Pumping Station
Impact Air Quality & Noise Monitoring Schedule (October 2023)

Sun	Mon	Tue	Wed	Thur	Fri	Sat
1 October	2	3 <ul style="list-style-type: none"> • Site Inspection • AQM • NM 	4	5	6	7
8	9 <ul style="list-style-type: none"> • Site Inspection 	10 <ul style="list-style-type: none"> • AQM • NM 	11	12	13	14 <ul style="list-style-type: none"> • AQM
15	16	17 <ul style="list-style-type: none"> • Site Inspection 	18	19	20 <ul style="list-style-type: none"> • AQM • NM 	21
22	23	24 <ul style="list-style-type: none"> • Site Inspection 	25	26 <ul style="list-style-type: none"> • AQM • NM 	27	28
29	30 <ul style="list-style-type: none"> • Site Inspection 	31				

Remarks

- Actual monitoring may be subjected to change due to any safety concern or adverse weather condition;
- Air Quality Monitoring(AQM): 3 x 1-hours TSP Monitoring in every 6 days;
Monitoring Locations: CA_M1(a) Construction Site Boundary near Hong Kong Baptist Theological Seminary (HKBTS) Staff & Students Quarters
- Noise Monitoring(NM): one set of Leq (30 min) between 0700 and 1900 hours on normal weekdays once a week;
Monitoring Locations: CN_M1 In front of the HKBTS Staff & Students Quarters
Monitoring Locations: CN_M2 In front of the HKBTS Administration and Education Block
- Site Inspection: Once a week
- The Air Quality Monitoring (AQM) and Noise Monitoring (NM) on 9th October 2023 were rescheduled to 10th October 2023 due to hoisting of Typhoon No. 8 NorthEast Gale Or Storm Signal.

Project: EP-597/2021 Sai O Trunk Sewer Sewage Pumping Station
Impact Air Quality & Noise Monitoring Schedule (November 2023)

Sun	Mon	Tue	Wed	Thur	Fri	Sat
29	30	31	1 November • AQM • NM	2	3	4
5	6	7 • AQM • NM	8 • Site Inspection	9	10	11
12	13 • Site Inspection • AQM • NM	14	15	16	17	18 • AQM
19	20 • Site Inspection	21	22	23	24 • AQM • NM	25
26	27 • Site Inspection	28	29	30 • AQM • NM	1	2

Remarks

- Actual monitoring may be subjected to change due to any safety concern or adverse weather condition;
- Air Quality Monitoring(AQM): 3 x 1-hours TSP Monitoring in every 6 days;
Monitoring Locations: CA_M1(a) Construction Site Boundary near Hong Kong Baptist Theological Seminary (HKBTS) Staff & Students Quarters
- Noise Monitoring(NM): one set of Leq (30 min) between 0700 and 1900 hours on normal weekdays once a week;
Monitoring Locations: CN_M1 In front of the HKBTS Staff & Students Quarters
Monitoring Locations: CN_M2 In front of the HKBTS Administration and Education Block
- Site Inspection: Once a week

Appendix E

Air Quality & Construction Noise
Monitoring Results

1-hr TSP Monitoring Results

Monitoring Location : CA_M1(a) Construction Site Boundary near Hong Kong Baptist Theological Seminary (HKBTS) Staff & Students Quarters

Start Date	Start Time	Weather Condition	Filter Identification No	Elapsed-Time Meter		Sampling Time (min)	Temperature (K)	Atmospheric Pressure (mmHg)	Filter Paper Weight			Flow Rate			Total Volume (m³)	Concentration			
				Start	Stop				Initial Weight	Final Weight	Particulate Weight	Intial	Final	Average		Value	Average	Action Level	Limit Level
3-Oct-23	13:00	Fine	M12315	6188.07	6248.07	60	302.3	758.0	2.7043	2.7145	0.010	1.13	1.13	1.13	67.82	150.4	139.0	339	500
	14:00	Fine	M12882	6248.07	6308.07	60	302.3	758.0	2.7266	2.7327	0.006	1.13	1.17	1.15	69.15	88.2			
	15:00	Fine	M12883	6308.07	6368.07	60	302.3	758.0	2.7330	2.7451	0.012	1.13	1.13	1.13	67.82	178.4			
10-Oct-23	9:11	Fine	M12891	6368.07	6428.07	60	298.3	761.8	2.7250	2.7318	0.007	1.28	1.28	1.28	76.90	88.4	55.1	339	500
	10:40	Fine	M12890	6428.07	6488.07	60	298.3	761.8	2.7359	2.7393	0.003	1.42	1.37	1.39	83.60	40.7			
	11:42	Fine	M12889	6488.07	6548.07	60	298.3	761.8	2.7313	2.7338	0.002	1.15	1.15	1.15	68.85	36.3			
14-Oct-23	9:31	Fine	M12122	6548.07	6608.07	60	299.6	760.0	2.6651	2.6745	0.009	1.14	1.14	1.14	68.47	137.3	100.0	339	500
	10:36	Fine	M12897	6608.07	6668.07	60	299.6	760.0	2.7312	2.7358	0.005	1.14	1.19	1.16	69.81	65.9			
	11:39	Fine	M12896	6668.07	6728.07	60	299.6	760.0	2.7190	2.7264	0.007	1.27	1.27	1.27	76.49	96.7			
20-Oct-23	9:40	Fine	M12900	6728.07	6788.07	60	298.9	761.5	2.7312	2.7369	0.006	1.15	1.15	1.15	68.71	83.0	74.1	339	500
	10:44	Fine	M12899	6788.07	6848.07	60	298.9	761.5	2.7245	2.7301	0.006	1.50	1.50	1.50	90.15	62.1			
	13:02	Fine	M12898	6848.07	6908.07	60	298.9	761.5	2.7310	2.7359	0.005	1.06	1.06	1.06	63.35	77.3			
26-Oct-23	9:02	Fine	M12084	6908.07	6968.07	60	299.2	761.0	2.8382	2.8475	0.009	1.14	1.14	1.14	68.62	135.5	146.3	339	500
	10:04	Fine	M12085	6968.07	7028.07	60	299.2	761.0	2.8415	2.8501	0.009	1.05	1.05	1.05	63.27	135.9			
	11:07	Fine	M12083	7028.07	7088.07	60	299.2	761.0	2.8219	2.8325	0.011	1.05	1.05	1.05	63.27	167.5			
															Min	36.3			
															Max	178.4			
															Average	102.9			

Report No. : 181172EN232604



Page 1 of 1

Test Report on Analysis of Filters**Information Supplied by Client**

Client : Fugro Technical Services Ltd.

Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.

Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station

Sample description : 3 samples of TSP filter paper

Sample identification : -

Sampling date : -

Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

Laboratory Information

Filter paper I.D. : M12315, M12882, M12883

Date of receipt of sample : 04/10/2023

Date test completed : 05/10/2023

Test method used : USEPA Method 40 CFR Part 50 Appendix B.

Results :

Filter paper I.D.	Initial wt. of filter, g	Final wt. of filter, g
M12315	2.7043	2.7145
M12882	2.7266	2.7327
M12883	2.7330	2.7451

Supervised by : C.H. Chiu

Certified by : Approved Signatory : HO Kin Man, John
Assistant General Manager – LaboratoriesDate : 6/10/2023
** End of Report ***Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.*

Report No. : 181172EN232604(1) 

Page 1 of 1

Test Report on Analysis of Filters

Information Supplied by Client

Client : Fugro Technical Services Ltd.
Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.
Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station
Sample description : 3 samples of TSP filter paper
Sample identification : -
Sampling date : -
Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

Laboratory Information

Filter paper I.D. : M12889, M12890, M12891
Date of receipt of sample : 10/10/2023
Date test completed : 12/10/2023
Test method used : USEPA Method 40 CFR Part 50 Appendix B.

Results :

Filter paper I.D.	Initial wt. of filter, g	Final wt. of filter, g
M12889	2.7313	2.7338
M12890	2.7359	2.7393
M12891	2.7250	2.7318

Supervised by : C.H. Chiu

Certified by : 
Approved Signatory: HO Kin Man, John
Director

Date
** End of Report **

Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.

Report No. : 181172EN232604(2)



Page 1 of 1

Test Report on Analysis of Filters**Information Supplied by Client**

Client : Fugro Technical Services Ltd.

Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.

Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station

Sample description : 3 samples of TSP filter paper

Sample identification : -

Sampling date : -

Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

Laboratory Information

Filter paper I.D. : M12122, M12896, M12897

Date of receipt of sample : 16/10/2023

Date test completed : 17/10/2023

Test method used : USEPA Method 40 CFR Part 50 Appendix B.

Results :

Filter paper I.D.	Initial wt. of filter, g	Final wt. of filter, g
M12122	2.6651	2.6745
M12896	2.7190	2.7264
M12897	2.7312	2.7358

Supervised by : K.F. Wong

Certified by :

Approved Signatory : HO Kin Man, John
Director

Date

** End of Report **

17/10/2023

Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.

Report No. : 181172EN232604(3)



Page 1 of 1

Test Report on Analysis of Filters**Information Supplied by Client**

Client : Fugro Technical Services Ltd.

Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.

Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station

Sample description : 3 samples of TSP filter paper

Sample identification : -

Sampling date : -

Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

Laboratory Information

Filter paper I.D. : M12898, M12899, M12900

Date of receipt of sample : 20/10/2023


Date test completed : 24/10/2023

Test method used : USEPA Method 40 CFR Part 50 Appendix B.

Results :

Filter paper I.D.	Initial wt. of filter, g	Final wt. of filter, g
M12898	2.7310	2.7359
M12899	2.7245	2.7301
M12900	2.7312	2.7369

Supervised by : C.H. Chiu

Certified by : 
Approved Signatory: HO Kin Man, John
DirectorDate : 1/11/2023
** End of Report ***Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.*

Report No. : 181172EN232604(4)



Page 1 of 1

Test Report on Analysis of Filters**Information Supplied by Client**

Client : Fugro Technical Services Ltd.

Client's address : 13/F, Fugro House – KCC2, No.1 Kwai On Road, Kwai Chung, N.T., H.K.

Project : Provision of ET Services for Sai O Trunk Sewer Sewage Pumping Station

Sample description : 3 samples of TSP filter paper

Sample identification : -

Sampling date : -

Test required : Provision of conditioned & tared filter paper and subsequent reconditioning and reweighing of returned filter paper for TSP monitoring

Laboratory Information

Filter paper I.D. : M12083, M12084, M12085

Date of receipt of sample : 26/10/2023

Date test completed : 28/10/2023

Test method used : USEPA Method 40 CFR Part 50 Appendix B.

Results :

Filter paper I.D.	Initial wt. of filter, g	Final wt. of filter, g
M12083	2.8219	2.8325
M12084	2.8382	2.8475
M12085	2.8415	2.8501

Supervised by : C.H. Chiu

Certified by : 
Approved Signatory : HO Kin Man, John
DirectorDate : 1/11/2023
** End of Report ***Note : This report refers only to the sample(s) tested and the result(s) applied to the sample(s) as received.*

Noise Monitoring Results

Monitoring Location : CN_M1 In front of the HKBTS Staff & Students Quarters

Date	Weather	Wind Speed (m/s)	Start Time	Noise Monitoring (30min)(dB(A))			
				Corrected Leq	Leq	L90	L10
3-Oct-23	Fine	0.3	13:10	62.4	59.4	56.5	63.5
10-Oct-23	Fine	0.3	9:41	61.2	58.2	53.0	62.5
20-Oct-23	Fine	0.3	9:51	63.9	60.9	55.5	63.0
26-Oct-23	Fine	0.3	8:32	61.4	58.4	55.0	60.5
Average :				62.4			
Baseline Level:				64.3			
Action Level :				When one valid documented complaint is received			
Limit Level :				70dB(A) for schools and 65dB(A) during school examination periods			

Monitoring Location : CN_M2 In front of the HKBTS Administration and Education Block


Date	Weather	Wind Speed (m/s)	Start Time	Noise Monitoring (30min)(dB(A))		
				Leq	L90	L10
3-Oct-23	Fine	0.2	13:58	58.2	56.0	60.0
10-Oct-23	Fine	0.4	10:29	56.4	54.0	58.0
20-Oct-23	Fine	0.2	10:49	58.9	49.5	60.5
26-Oct-23	Fine	0.4	9:11	54.7	52.0	63.0
Average :				57.3		
Baseline Level:				62.5		
Action Level :				When one valid documented complaint is received		
Limit Level :				70dB(A) for schools and 65dB(A) during school examination periods		

Remarks: 1. Noise results at CN_M1 were calculated by +3 dB (A) correction for free-field measurement.



Appendix F

Air Quality & Construction Noise
Monitoring Graphs

1-hr TSP Monitoring Graph

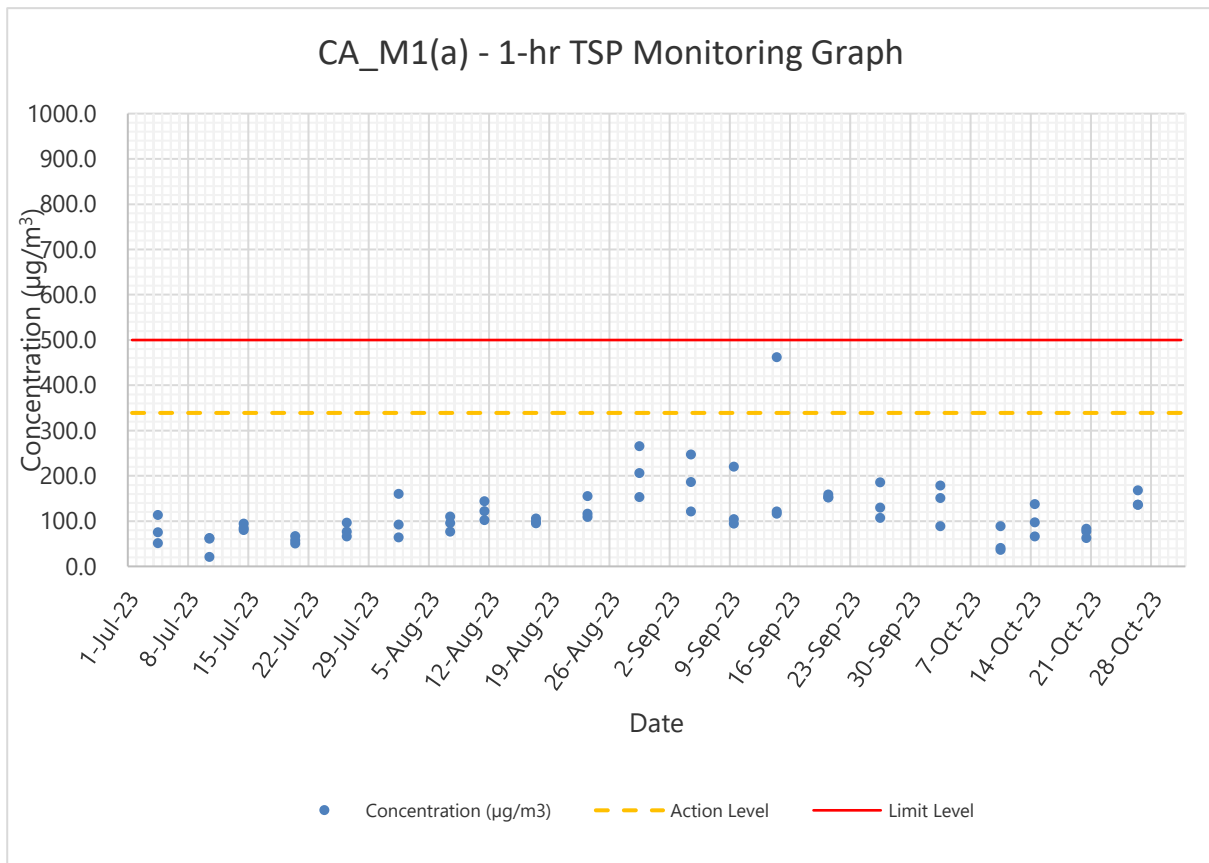

Noise Monitoring Graph

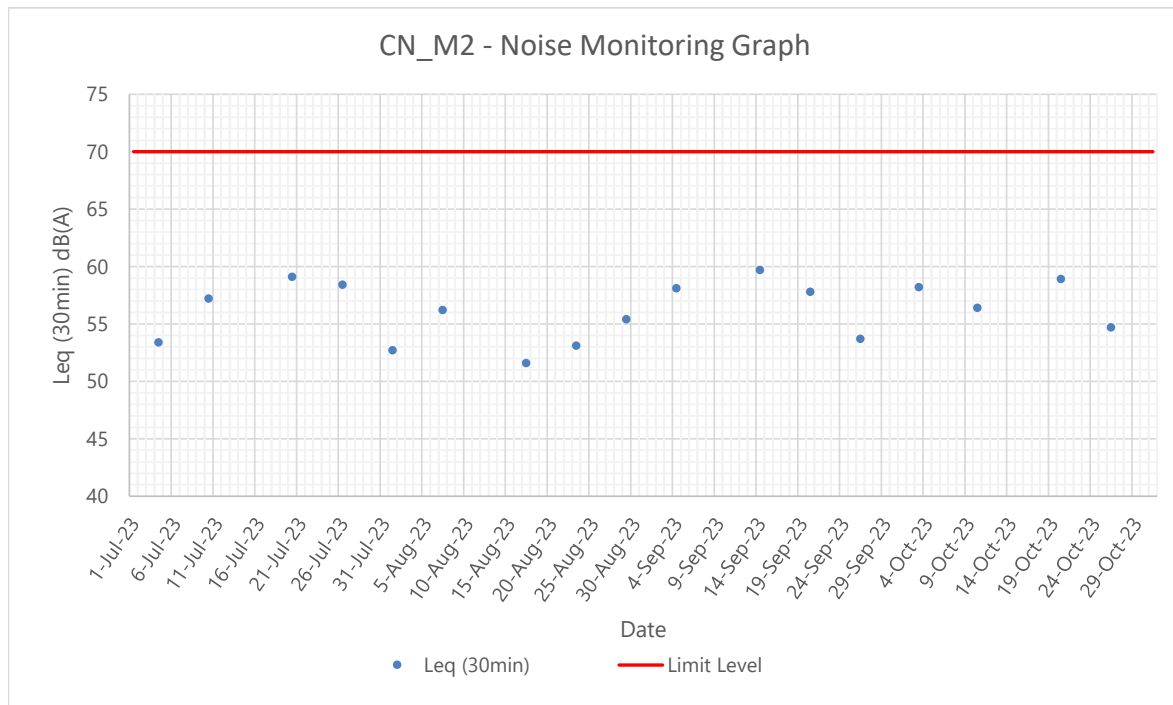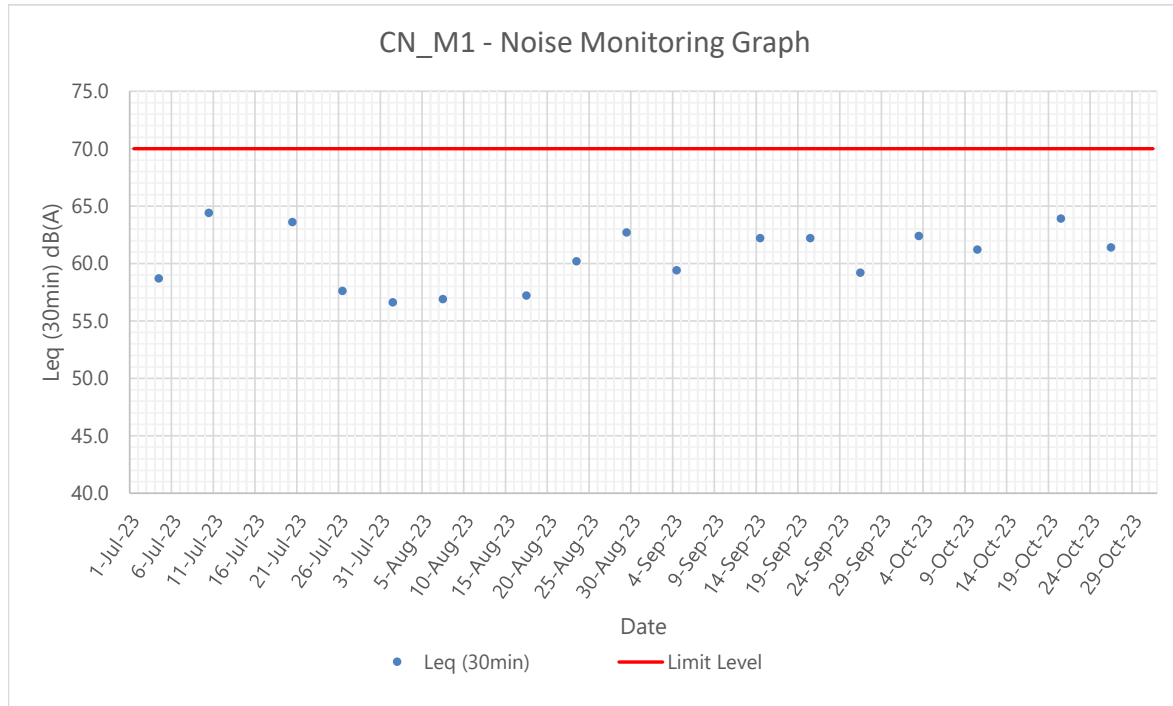

Appendix G

Action and Limit Level

Action and Limit Levels for Air Quality

Monitoring Parameter	Monitoring Station	Action Level	Limit Level
1-hour TSP	CA_M1(a)	339 $\mu\text{g}/\text{m}^3$	500 $\mu\text{g}/\text{m}^3$

Action and Limit Levels for Construction Noise

Monitoring Parameter	Monitoring Station	Action Level	Limit Level
0700-1900 hours in normal weekdays LA_{eq} (30min)	CN_M1	When one documented complaint is received	70dB(A) during normal teaching period & 65 dB(A) during examination periods
	CN_M2		

Remark:

CN_M1: Free-field measurement (+3 dB(A) correction has been applied).

Appendix H

Event and Action Plan

Event and Action Plan for Air Quality (Construction Dust)

EVENT	ACTION			
	ET	IEC	ER	Contractor
Action level being exceeded by one sampling	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of complaint and propose remedial measures; 2. Inform Contractor, IEC and ER; 3. Repeat measurement to confirm finding; and 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; and 3. Review and advise the ET and ER on the effectiveness of the proposed remedial measures. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Identify source(s), investigate the causes of exceedance and propose remedial measures; 2. Implement remedial measures; and 3. Amend working methods agreed with the ER as appropriate.
Action level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> 1. Identify source; 2. Inform Contractor, IEC and ER; 3. Advise the Contractor and ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with Contractor, IEC and ER; and 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET, ER and Contractor on possible remedial measures; 4. Advise the ET and ER on the effectiveness of the proposed remedial measures; and 5. Supervise Implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Identify source and investigate the causes of exceedance; 2. Submit proposals for remedial measures to the ER with a copy to ET and IEC within three working days of notification; 3. Implement the agreed proposals; and 4. Amend proposal as appropriate.
Limit level being exceeded by one sampling	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform Contractor, IEC, ER, and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; and 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; and 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Identify source(s) and investigate the causes of exceedance; 2. Take immediate action to avoid further exceedance; 3. Submit proposals for remedial measures to ER with a copy to ET and IEC within three working days of notification; 4. Implement the agreed proposals; and 5. Amend proposal if appropriate.
Limit level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> 1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET; 2. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 3. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and 4. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented; 3. Supervise the implementation of remedial measures; and 4. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Identify source(s) and investigate the causes of exceedance; 2. Take immediate action to avoid further exceedance; 3. Submit proposals for remedial measures to the ER with a copy to the IEC and ET within three working days of notification; 4. Implement the agreed proposals; 5. Revise and resubmit proposals if problem still not under control; and 6. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Event and Action Plan for Noise (Construction Noise)

EVENT	ACTION			
	ET	IEC	ER	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; and 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analyzed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; and 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analyzed noise problem; and 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC; and 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC, ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analyzed noise problem; 4. Ensure remedial measures properly implemented; and 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; and 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Appendix I

Weather and Meteorological

Conditions during Reporting Month

Weather Condition (October 2023)

Date	Mean Pressure (hPa)	Air Temperature			Mean Relative Humidity (%)	Total Rainfall (mm)
		Maximum (°C)	Mean (°C)	Minimum (°C)		
1 October 2023	1009.8	34.0	30.0	28.0	77	0
2 October 2023	1011.3	32.3	29.5	27.9	76	0.4
3 October 2023	1010.6	31.4	29.3	27.7	78	Trace
4 October 2023	1009.0	34.6	30.8	28.3	73	0
5 October 2023	1007.3	34.1	30.5	28.5	58	0
6 October 2023	1008.3	32.2	28.3	26.7	62	Trace
7 October 2023	1008.1	27.2	25.1	23.5	74	1.9
8 October 2023	1008.1	25.1	24.2	22.7	87	92.2
9 October 2023	1013.2	25.0	24.5	23.4	94	369.7
10 October 2023	1015.6	26.9	25.3	23.8	83	2.3
11 October 2023	1016.9	29.2	25.6	23.7	75	0
12 October 2023	1017.6	29.2	25.7	23.5	72	0
13 October 2023	1015.5	30.2	26.7	24.8	67	0
14 October 2023	1013.2	30.0	26.6	24.7	66	0
15 October 2023	1013.3	29.9	26.9	25.1	72	0.1
16 October 2023	1014.9	28.9	26.5	25.4	70	0
17 October 2023	1015.4	28.2	25.8	24.5	61	Trace
18 October 2023	1015.2	25.4	24.6	23.4	85	38.3
19 October 2023	1014.7	26.0	25.3	24.6	91	27.9
20 October 2023	1015.2	27.6	25.9	24.6	82	0.2
21 October 2023	1018.4	25.4	23.3	22.0	76	Trace
22 October 2023	1018.8	27.8	24.5	22.4	71	Trace
23 October 2023	1017.4	29.4	26.0	23.8	77	Trace
24 October 2023	1016.3	30.1	26.8	24.8	76	0
25 October 2023	1015.5	29.7	26.6	25.3	80	0
26 October 2023	1014.6	29.2	26.2	24.8	78	0
27 October 2023	1014.0	29.6	26.6	24.9	81	0
28 October 2023	1014.8	27.7	25.8	24.2	85	9.5
29 October 2023	1016.1	27.1	25.3	24.1	79	3.5
30 October 2023	1017.1	29.3	26.1	24.6	77	Trace
31 October 2023	1018.4	28.6	25.8	24.1	70	0

Remark:

- Trace means rainfall less than 0.05 mm.

Source: Hong Kong Observatory

Appendix J

Wind Data

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
01 Oct 2023 00:00	2.7	NEN	02 Oct 2023 00:00	5.1	NE
01 Oct 2023 01:00	2.7	NE	02 Oct 2023 01:00	3.8	E
01 Oct 2023 02:00	2.7	NEN	02 Oct 2023 02:00	6.8	N
01 Oct 2023 03:00	2.7	SWS	02 Oct 2023 03:00	6.8	N
01 Oct 2023 04:00	2.7	SEE	02 Oct 2023 04:00	4.7	NEE
01 Oct 2023 05:00	2.7	NE	02 Oct 2023 05:00	2.7	NEN
01 Oct 2023 06:00	2.7	NEE	02 Oct 2023 06:00	4.6	NEN
01 Oct 2023 07:00	2.7	E	02 Oct 2023 07:00	4.8	NEN
01 Oct 2023 08:00	2.6	NE	02 Oct 2023 08:00	7.4	N
01 Oct 2023 09:00	2.6	N	02 Oct 2023 09:00	6.3	N
01 Oct 2023 10:00	2.7	NEE	02 Oct 2023 10:00	3.8	NEN
01 Oct 2023 11:00	2.7	SW	02 Oct 2023 11:00	2.7	NEN
01 Oct 2023 12:00	2.6	NE	02 Oct 2023 12:00	2.7	NEE
01 Oct 2023 13:00	3.1	E	02 Oct 2023 13:00	3.5	NEN
01 Oct 2023 14:00	5.4	N	02 Oct 2023 14:00	2.8	NEE
01 Oct 2023 15:00	6.6	N	02 Oct 2023 15:00	3.5	N
01 Oct 2023 16:00	3.0	NEN	02 Oct 2023 16:00	4.0	NEN
01 Oct 2023 17:00	6.7	N	02 Oct 2023 17:00	3.0	NEN
01 Oct 2023 18:00	5.9	NEN	02 Oct 2023 18:00	3.9	N
01 Oct 2023 19:00	3.5	N	02 Oct 2023 19:00	2.7	N
01 Oct 2023 20:00	3.3	NE	02 Oct 2023 20:00	2.6	NE
01 Oct 2023 21:00	2.9	NEN	02 Oct 2023 21:00	2.7	NEN
01 Oct 2023 22:00	6.9	NEN	02 Oct 2023 22:00	2.7	NEN
01 Oct 2023 23:00	4.2	N	02 Oct 2023 23:00	2.7	NEE

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
03 Oct 2023 00:00	2.7	NE	04 Oct 2023 00:00	3.6	NWW
03 Oct 2023 01:00	2.7	NE	04 Oct 2023 01:00	2.7	NWW
03 Oct 2023 02:00	2.7	NE	04 Oct 2023 02:00	2.7	NWW
03 Oct 2023 03:00	2.7	NEN	04 Oct 2023 03:00	2.7	W
03 Oct 2023 04:00	2.6	N	04 Oct 2023 04:00	2.7	W
03 Oct 2023 05:00	2.7	N	04 Oct 2023 05:00	2.7	SWW
03 Oct 2023 06:00	2.7	N	04 Oct 2023 06:00	2.7	W
03 Oct 2023 07:00	3.1	N	04 Oct 2023 07:00	2.7	W
03 Oct 2023 08:00	3.6	NEN	04 Oct 2023 08:00	2.7	NW
03 Oct 2023 09:00	2.7	SEE	04 Oct 2023 09:00	2.7	NEN
03 Oct 2023 10:00	2.7	SE	04 Oct 2023 10:00	2.6	NEE
03 Oct 2023 11:00	2.7	S	04 Oct 2023 11:00	2.7	NE
03 Oct 2023 12:00	2.7	N	04 Oct 2023 12:00	2.7	NW
03 Oct 2023 13:00	3.4	NEN	04 Oct 2023 13:00	2.7	SW
03 Oct 2023 14:00	4.2	N	04 Oct 2023 14:00	2.7	NWW
03 Oct 2023 15:00	4.8	NEN	04 Oct 2023 15:00	3.9	W
03 Oct 2023 16:00	6.8	N	04 Oct 2023 16:00	2.8	SWW
03 Oct 2023 17:00	2.7	NEN	04 Oct 2023 17:00	2.7	W
03 Oct 2023 18:00	2.7	NEE	04 Oct 2023 18:00	2.7	SWW
03 Oct 2023 19:00	3.2	E	04 Oct 2023 19:00	2.7	SEE
03 Oct 2023 20:00	2.7	W	04 Oct 2023 20:00	2.7	SEE
03 Oct 2023 21:00	3.5	W	04 Oct 2023 21:00	3.1	SE
03 Oct 2023 22:00	3.0	SWW	04 Oct 2023 22:00	2.7	NE
03 Oct 2023 23:00	2.8	NWW	04 Oct 2023 23:00	3.7	NEN

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
05 Oct 2023 00:00	2.7	SWS	06 Oct 2023 00:00	6.4	NEN
05 Oct 2023 01:00	2.7	NEN	06 Oct 2023 01:00	4.2	SE
05 Oct 2023 02:00	2.8	S	06 Oct 2023 02:00	3.8	SE
05 Oct 2023 03:00	2.7	SW	06 Oct 2023 03:00	2.7	NEE
05 Oct 2023 04:00	3.2	NWW	06 Oct 2023 04:00	3.8	NWW
05 Oct 2023 05:00	3.0	SE	06 Oct 2023 05:00	2.7	E
05 Oct 2023 06:00	3.2	SEE	06 Oct 2023 06:00	2.8	N
05 Oct 2023 07:00	2.7	S	06 Oct 2023 07:00	5.1	NEE
05 Oct 2023 08:00	2.7	NE	06 Oct 2023 08:00	4.4	SES
05 Oct 2023 09:00	5.1	NEE	06 Oct 2023 09:00	2.8	E
05 Oct 2023 10:00	2.7	NWW	06 Oct 2023 10:00	2.7	NE
05 Oct 2023 11:00	3.4	SEE	06 Oct 2023 11:00	3.5	NEE
05 Oct 2023 12:00	2.9	NE	06 Oct 2023 12:00	2.9	NEE
05 Oct 2023 13:00	3.0	S	06 Oct 2023 13:00	3.1	SWS
05 Oct 2023 14:00	3.9	S	06 Oct 2023 14:00	2.7	E
05 Oct 2023 15:00	4.5	NE	06 Oct 2023 15:00	3.6	E
05 Oct 2023 16:00	3.8	SWS	06 Oct 2023 16:00	5.7	N
05 Oct 2023 17:00	2.9	NEE	06 Oct 2023 17:00	2.9	SW
05 Oct 2023 18:00	4.7	NEE	06 Oct 2023 18:00	5.2	W
05 Oct 2023 19:00	3.3	SEE	06 Oct 2023 19:00	3.5	SW
05 Oct 2023 20:00	5.3	E	06 Oct 2023 20:00	3.1	SES
05 Oct 2023 21:00	3.1	NEN	06 Oct 2023 21:00	3.7	NW
05 Oct 2023 22:00	3.9	SEE	06 Oct 2023 22:00	7.0	S
05 Oct 2023 23:00	3.6	S	06 Oct 2023 23:00	5.3	SEE

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
07 Oct 2023 00:00	5.0	NW	08 Oct 2023 00:00	7.0	NEE
07 Oct 2023 01:00	6.3	SWS	08 Oct 2023 01:00	8.0	SE
07 Oct 2023 02:00	2.8	SWS	08 Oct 2023 02:00	3.1	E
07 Oct 2023 03:00	7.0	SE	08 Oct 2023 03:00	3.2	N
07 Oct 2023 04:00	6.0	SES	08 Oct 2023 04:00	2.8	NE
07 Oct 2023 05:00	4.4	S	08 Oct 2023 05:00	8.3	NE
07 Oct 2023 06:00	5.8	SE	08 Oct 2023 06:00	8.6	NEN
07 Oct 2023 07:00	5.2	E	08 Oct 2023 07:00	14.2	NE
07 Oct 2023 08:00	3.7	S	08 Oct 2023 08:00	11.6	NEN
07 Oct 2023 09:00	4.1	SE	08 Oct 2023 09:00	4.9	E
07 Oct 2023 10:00	3.2	SES	08 Oct 2023 10:00	6.6	NEN
07 Oct 2023 11:00	5.1	SW	08 Oct 2023 11:00	6.7	E
07 Oct 2023 12:00	3.6	SW	08 Oct 2023 12:00	11.7	NEN
07 Oct 2023 13:00	3.6	SES	08 Oct 2023 13:00	11.6	NEN
07 Oct 2023 14:00	2.8	NWW	08 Oct 2023 14:00	4.4	NEN
07 Oct 2023 15:00	3.0	S	08 Oct 2023 15:00	6.5	NE
07 Oct 2023 16:00	6.2	SW	08 Oct 2023 16:00	6.2	NE
07 Oct 2023 17:00	3.0	SW	08 Oct 2023 17:00	5.7	NEN
07 Oct 2023 18:00	3.0	E	08 Oct 2023 18:00	5.5	NEN
07 Oct 2023 19:00	3.9	NWW	08 Oct 2023 19:00	4.3	SW
07 Oct 2023 20:00	3.3	S	08 Oct 2023 20:00	4.1	E
07 Oct 2023 21:00	3.5	NE	08 Oct 2023 21:00	4.1	NEN
07 Oct 2023 22:00	5.5	SES	08 Oct 2023 22:00	4.7	E
07 Oct 2023 23:00	5.3	S	08 Oct 2023 23:00	3.8	N

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
09 Oct 2023 00:00	3.9	N	10 Oct 2023 00:00	2.7	NE
09 Oct 2023 01:00	5.1	NE	10 Oct 2023 01:00	3.1	SW
09 Oct 2023 02:00	3.7	NEE	10 Oct 2023 02:00	3.3	E
09 Oct 2023 03:00	3.8	NE	10 Oct 2023 03:00	2.9	E
09 Oct 2023 04:00	4.0	NE	10 Oct 2023 04:00	2.8	NE
09 Oct 2023 05:00	3.9	NEN	10 Oct 2023 05:00	3.2	NEN
09 Oct 2023 06:00	3.4	NEN	10 Oct 2023 06:00	2.8	NE
09 Oct 2023 07:00	3.7	SEE	10 Oct 2023 07:00	2.7	NEN
09 Oct 2023 08:00	3.6	SEE	10 Oct 2023 08:00	2.7	NEN
09 Oct 2023 09:00	3.0	NEE	10 Oct 2023 09:00	2.7	NEE
09 Oct 2023 10:00	3.1	NE	10 Oct 2023 10:00	2.7	NEE
09 Oct 2023 11:00	3.0	SE	10 Oct 2023 11:00	2.6	NEN
09 Oct 2023 12:00	3.0	SWS	10 Oct 2023 12:00	2.7	NE
09 Oct 2023 13:00	3.0	W	10 Oct 2023 13:00	2.7	NW
09 Oct 2023 14:00	3.0	NWW	10 Oct 2023 14:00	2.8	E
09 Oct 2023 15:00	3.0	S	10 Oct 2023 15:00	2.7	NEN
09 Oct 2023 16:00	3.1	NEN	10 Oct 2023 16:00	2.7	NEE
09 Oct 2023 17:00	3.4	SEE	10 Oct 2023 17:00	2.7	NEN
09 Oct 2023 18:00	3.2	E	10 Oct 2023 18:00	2.7	NE
09 Oct 2023 19:00	2.9	NEN	10 Oct 2023 19:00	2.7	NEN
09 Oct 2023 20:00	2.8	SE	10 Oct 2023 20:00	2.7	E
09 Oct 2023 21:00	2.8	NE	10 Oct 2023 21:00	2.7	E
09 Oct 2023 22:00	2.8	NEN	10 Oct 2023 22:00	2.7	NE
09 Oct 2023 23:00	2.9	E	10 Oct 2023 23:00	2.7	NEE

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
11 Oct 2023 00:00	2.7	NEN	12 Oct 2023 00:00	2.7	NEN
11 Oct 2023 01:00	3.1	NEN	12 Oct 2023 01:00	2.7	NEE
11 Oct 2023 02:00	3.3	SE	12 Oct 2023 02:00	2.7	NEN
11 Oct 2023 03:00	3.7	NEN	12 Oct 2023 03:00	2.7	NE
11 Oct 2023 04:00	2.7	SE	12 Oct 2023 04:00	2.7	NE
11 Oct 2023 05:00	3.0	N	12 Oct 2023 05:00	2.7	NEE
11 Oct 2023 06:00	2.7	NEN	12 Oct 2023 06:00	2.7	NEE
11 Oct 2023 07:00	3.0	NE	12 Oct 2023 07:00	2.7	NE
11 Oct 2023 08:00	2.7	SE	12 Oct 2023 08:00	2.6	E
11 Oct 2023 09:00	2.7	NEE	12 Oct 2023 09:00	2.6	NE
11 Oct 2023 10:00	4.0	NEN	12 Oct 2023 10:00	2.7	E
11 Oct 2023 11:00	5.4	SE	12 Oct 2023 11:00	2.7	NEE
11 Oct 2023 12:00	4.6	NEN	12 Oct 2023 12:00	2.7	NEE
11 Oct 2023 13:00	5.0	NEE	12 Oct 2023 13:00	2.6	NEN
11 Oct 2023 14:00	3.4	SE	12 Oct 2023 14:00	2.7	NEN
11 Oct 2023 15:00	5.0	SEE	12 Oct 2023 15:00	2.6	E
11 Oct 2023 16:00	3.7	NE	12 Oct 2023 16:00	2.7	N
11 Oct 2023 17:00	3.3	NEE	12 Oct 2023 17:00	2.6	NEE
11 Oct 2023 18:00	2.7	SES	12 Oct 2023 18:00	2.7	N
11 Oct 2023 19:00	2.7	NEN	12 Oct 2023 19:00	2.9	SE
11 Oct 2023 20:00	2.7	E	12 Oct 2023 20:00	2.6	NEN
11 Oct 2023 21:00	2.7	N	12 Oct 2023 21:00	2.7	E
11 Oct 2023 22:00	2.7	NEE	12 Oct 2023 22:00	2.7	E
11 Oct 2023 23:00	2.7	NEN	12 Oct 2023 23:00	2.7	E

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
13 Oct 2023 00:00	3.6	NEN	14 Oct 2023 00:00	2.7	NE
13 Oct 2023 01:00	2.7	NEN	14 Oct 2023 01:00	2.6	S
13 Oct 2023 02:00	2.7	E	14 Oct 2023 02:00	2.6	NEE
13 Oct 2023 03:00	2.7	NEN	14 Oct 2023 03:00	2.7	NW
13 Oct 2023 04:00	2.7	N	14 Oct 2023 04:00	2.7	NWW
13 Oct 2023 05:00	3.1	NEN	14 Oct 2023 05:00	2.7	SWW
13 Oct 2023 06:00	3.0	NEN	14 Oct 2023 06:00	2.7	SWW
13 Oct 2023 07:00	2.8	NE	14 Oct 2023 07:00	2.7	SE
13 Oct 2023 08:00	2.7	NE	14 Oct 2023 08:00	2.6	NEN
13 Oct 2023 09:00	2.8	NE	14 Oct 2023 09:00	2.7	SES
13 Oct 2023 10:00	2.9	NEN	14 Oct 2023 10:00	2.6	E
13 Oct 2023 11:00	2.6	NEE	14 Oct 2023 11:00	2.7	NEN
13 Oct 2023 12:00	2.7	SEE	14 Oct 2023 12:00	2.7	NEE
13 Oct 2023 13:00	2.7	SEE	14 Oct 2023 13:00	2.6	N
13 Oct 2023 14:00	2.7	SWS	14 Oct 2023 14:00	2.7	NE
13 Oct 2023 15:00	2.7	SW	14 Oct 2023 15:00	2.7	NEE
13 Oct 2023 16:00	2.7	SWS	14 Oct 2023 16:00	2.9	NEE
13 Oct 2023 17:00	2.9	NEN	14 Oct 2023 17:00	8.3	NEN
13 Oct 2023 18:00	2.7	NEN	14 Oct 2023 18:00	5.2	N
13 Oct 2023 19:00	2.7	NEE	14 Oct 2023 19:00	2.7	NEE
13 Oct 2023 20:00	2.7	NEE	14 Oct 2023 20:00	2.6	SE
13 Oct 2023 21:00	4.4	E	14 Oct 2023 21:00	2.7	SE
13 Oct 2023 22:00	2.7	NEN	14 Oct 2023 22:00	2.7	SEE
13 Oct 2023 23:00	3.3	NEN	14 Oct 2023 23:00	2.7	SEE

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
15 Oct 2023 00:00	2.7	SEE	16 Oct 2023 00:00	2.7	NEN
15 Oct 2023 01:00	2.7	SEE	16 Oct 2023 01:00	2.7	NEN
15 Oct 2023 02:00	2.6	SEE	16 Oct 2023 02:00	3.3	N
15 Oct 2023 03:00	2.7	SEE	16 Oct 2023 03:00	2.8	NEN
15 Oct 2023 04:00	2.7	SEE	16 Oct 2023 04:00	2.7	SE
15 Oct 2023 05:00	2.7	SEE	16 Oct 2023 05:00	2.8	NE
15 Oct 2023 06:00	2.7	SEE	16 Oct 2023 06:00	3.3	E
15 Oct 2023 07:00	2.6	SE	16 Oct 2023 07:00	4.1	NEN
15 Oct 2023 08:00	2.8	NEN	16 Oct 2023 08:00	2.7	SE
15 Oct 2023 09:00	2.7	NEN	16 Oct 2023 09:00	4.4	NEN
15 Oct 2023 10:00	2.7	NEN	16 Oct 2023 10:00	2.7	N
15 Oct 2023 11:00	2.7	SES	16 Oct 2023 11:00	2.7	N
15 Oct 2023 12:00	2.7	SWS	16 Oct 2023 12:00	3.1	NE
15 Oct 2023 13:00	2.6	E	16 Oct 2023 13:00	4.0	E
15 Oct 2023 14:00	2.9	NEE	16 Oct 2023 14:00	2.8	N
15 Oct 2023 15:00	4.0	N	16 Oct 2023 15:00	3.9	NE
15 Oct 2023 16:00	3.5	NEN	16 Oct 2023 16:00	5.9	NEN
15 Oct 2023 17:00	3.6	NEN	16 Oct 2023 17:00	2.7	N
15 Oct 2023 18:00	3.4	N	16 Oct 2023 18:00	2.7	NEN
15 Oct 2023 19:00	3.0	NEN	16 Oct 2023 19:00	3.4	N
15 Oct 2023 20:00	2.7	NEN	16 Oct 2023 20:00	6.2	N
15 Oct 2023 21:00	2.7	NE	16 Oct 2023 21:00	4.8	N
15 Oct 2023 22:00	2.7	NE	16 Oct 2023 22:00	3.3	NEE
15 Oct 2023 23:00	2.9	NEN	16 Oct 2023 23:00	4.6	NEN

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
17 Oct 2023 00:00	3.0	NEN	18 Oct 2023 00:00	4.2	NEE
17 Oct 2023 01:00	2.9	NEE	18 Oct 2023 01:00	4.3	NEN
17 Oct 2023 02:00	2.7	NEN	18 Oct 2023 02:00	4.7	NEN
17 Oct 2023 03:00	3.3	NEN	18 Oct 2023 03:00	3.7	NE
17 Oct 2023 04:00	3.9	NEN	18 Oct 2023 04:00	7.9	N
17 Oct 2023 05:00	4.0	NE	18 Oct 2023 05:00	4.4	NEN
17 Oct 2023 06:00	3.8	NE	18 Oct 2023 06:00	7.7	NE
17 Oct 2023 07:00	2.7	NEE	18 Oct 2023 07:00	6.6	NEN
17 Oct 2023 08:00	3.2	NE	18 Oct 2023 08:00	3.1	NE
17 Oct 2023 09:00	2.8	N	18 Oct 2023 09:00	4.2	NEE
17 Oct 2023 10:00	3.4	NEN	18 Oct 2023 10:00	3.5	SW
17 Oct 2023 11:00	2.7	SEE	18 Oct 2023 11:00	3.0	E
17 Oct 2023 12:00	3.1	N	18 Oct 2023 12:00	3.4	E
17 Oct 2023 13:00	3.6	NE	18 Oct 2023 13:00	2.8	E
17 Oct 2023 14:00	2.7	NEN	18 Oct 2023 14:00	10.2	NEE
17 Oct 2023 15:00	3.5	NEN	18 Oct 2023 15:00	5.4	SWS
17 Oct 2023 16:00	4.5	NEN	18 Oct 2023 16:00	4.0	S
17 Oct 2023 17:00	7.3	NEN	18 Oct 2023 17:00	2.9	SE
17 Oct 2023 18:00	2.8	NEE	18 Oct 2023 18:00	3.4	SEE
17 Oct 2023 19:00	2.7	NE	18 Oct 2023 19:00	7.4	NEN
17 Oct 2023 20:00	2.8	NEN	18 Oct 2023 20:00	7.5	SES
17 Oct 2023 21:00	2.7	NE	18 Oct 2023 21:00	4.0	E
17 Oct 2023 22:00	4.6	NE	18 Oct 2023 22:00	3.5	NE
17 Oct 2023 23:00	7.4	NE	18 Oct 2023 23:00	3.2	E

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
19 Oct 2023 00:00	4.1	NEE	20 Oct 2023 00:00	2.7	NEN
19 Oct 2023 01:00	6.0	NEN	20 Oct 2023 01:00	2.7	NEE
19 Oct 2023 02:00	4.2	SE	20 Oct 2023 02:00	2.7	E
19 Oct 2023 03:00	2.9	NEE	20 Oct 2023 03:00	2.6	NE
19 Oct 2023 04:00	3.2	NE	20 Oct 2023 04:00	2.7	NE
19 Oct 2023 05:00	3.0	N	20 Oct 2023 05:00	2.7	NEE
19 Oct 2023 06:00	2.7	NEN	20 Oct 2023 06:00	2.7	N
19 Oct 2023 07:00	2.7	NE	20 Oct 2023 07:00	2.7	NEN
19 Oct 2023 08:00	3.1	N	20 Oct 2023 08:00	2.7	NE
19 Oct 2023 09:00	2.7	NEN	20 Oct 2023 09:00	2.7	E
19 Oct 2023 10:00	2.8	NEE	20 Oct 2023 10:00	2.7	N
19 Oct 2023 11:00	2.7	NEE	20 Oct 2023 11:00	4.5	SE
19 Oct 2023 12:00	2.7	E	20 Oct 2023 12:00	4.2	NEE
19 Oct 2023 13:00	2.7	NEE	20 Oct 2023 13:00	2.7	N
19 Oct 2023 14:00	2.7	NEE	20 Oct 2023 14:00	2.7	SES
19 Oct 2023 15:00	2.7	NEE	20 Oct 2023 15:00	2.8	S
19 Oct 2023 16:00	2.7	E	20 Oct 2023 16:00	2.7	NEN
19 Oct 2023 17:00	3.1	NEN	20 Oct 2023 17:00	2.7	E
19 Oct 2023 18:00	2.7	SE	20 Oct 2023 18:00	2.7	NEN
19 Oct 2023 19:00	2.7	NEE	20 Oct 2023 19:00	3.0	SES
19 Oct 2023 20:00	3.2	NE	20 Oct 2023 20:00	2.7	NEN
19 Oct 2023 21:00	4.6	NE	20 Oct 2023 21:00	2.7	SEE
19 Oct 2023 22:00	2.7	E	20 Oct 2023 22:00	2.7	N
19 Oct 2023 23:00	2.7	NEE	20 Oct 2023 23:00	2.8	NE

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
21 Oct 2023 00:00	2.8	NE	22 Oct 2023 00:00	2.7	NE
21 Oct 2023 01:00	2.7	NEN	22 Oct 2023 01:00	2.7	N
21 Oct 2023 02:00	2.7	SE	22 Oct 2023 02:00	2.7	N
21 Oct 2023 03:00	2.7	E	22 Oct 2023 03:00	2.7	W
21 Oct 2023 04:00	3.4	NE	22 Oct 2023 04:00	2.7	W
21 Oct 2023 05:00	2.7	N	22 Oct 2023 05:00	2.7	N
21 Oct 2023 06:00	2.7	SES	22 Oct 2023 06:00	2.7	NE
21 Oct 2023 07:00	3.4	N	22 Oct 2023 07:00	2.7	N
21 Oct 2023 08:00	2.7	SEE	22 Oct 2023 08:00	2.7	SEE
21 Oct 2023 09:00	2.7	NEN	22 Oct 2023 09:00	2.7	N
21 Oct 2023 10:00	2.7	NE	22 Oct 2023 10:00	2.6	SW
21 Oct 2023 11:00	2.7	NEN	22 Oct 2023 11:00	2.7	N
21 Oct 2023 12:00	2.9	N	22 Oct 2023 12:00	2.7	NEN
21 Oct 2023 13:00	3.3	NEN	22 Oct 2023 13:00	2.7	NEE
21 Oct 2023 14:00	3.4	NE	22 Oct 2023 14:00	2.7	E
21 Oct 2023 15:00	3.9	N	22 Oct 2023 15:00	2.7	NE
21 Oct 2023 16:00	3.6	N	22 Oct 2023 16:00	2.7	E
21 Oct 2023 17:00	2.8	NEE	22 Oct 2023 17:00	2.7	NE
21 Oct 2023 18:00	2.7	NEN	22 Oct 2023 18:00	2.7	SEE
21 Oct 2023 19:00	2.9	NEE	22 Oct 2023 19:00	2.9	SE
21 Oct 2023 20:00	2.8	SEE	22 Oct 2023 20:00	2.7	SEE
21 Oct 2023 21:00	2.7	NEN	22 Oct 2023 21:00	2.8	E
21 Oct 2023 22:00	2.7	NEE	22 Oct 2023 22:00	2.7	N
21 Oct 2023 23:00	2.7	NEE	22 Oct 2023 23:00	2.7	NEN

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
23 Oct 2023 00:00	2.7	NEN	24 Oct 2023 00:00	2.7	NE
23 Oct 2023 01:00	2.7	N	24 Oct 2023 01:00	2.7	NE
23 Oct 2023 02:00	2.7	N	24 Oct 2023 02:00	2.7	NE
23 Oct 2023 03:00	2.7	N	24 Oct 2023 03:00	2.7	NEN
23 Oct 2023 04:00	2.7	S	24 Oct 2023 04:00	2.6	N
23 Oct 2023 05:00	2.7	NEN	24 Oct 2023 05:00	2.7	N
23 Oct 2023 06:00	2.7	NEN	24 Oct 2023 06:00	2.7	N
23 Oct 2023 07:00	2.7	NEE	24 Oct 2023 07:00	2.7	NEN
23 Oct 2023 08:00	2.7	SEE	24 Oct 2023 08:00	2.7	NEN
23 Oct 2023 09:00	2.7	NEN	24 Oct 2023 09:00	2.7	NE
23 Oct 2023 10:00	2.7	S	24 Oct 2023 10:00	2.7	SE
23 Oct 2023 11:00	2.7	NEN	24 Oct 2023 11:00	2.7	NEN
23 Oct 2023 12:00	2.7	NE	24 Oct 2023 12:00	2.7	NEN
23 Oct 2023 13:00	2.6	NE	24 Oct 2023 13:00	2.7	N
23 Oct 2023 14:00	2.6	NEN	24 Oct 2023 14:00	2.7	NE
23 Oct 2023 15:00	2.6	S	24 Oct 2023 15:00	2.7	NEN
23 Oct 2023 16:00	2.7	SE	24 Oct 2023 16:00	2.7	NEN
23 Oct 2023 17:00	2.7	N	24 Oct 2023 17:00	2.6	NEN
23 Oct 2023 18:00	2.7	N	24 Oct 2023 18:00	2.7	N
23 Oct 2023 19:00	2.7	NE	24 Oct 2023 19:00	2.7	NE
23 Oct 2023 20:00	2.7	NEN	24 Oct 2023 20:00	2.7	N
23 Oct 2023 21:00	2.7	NEN	24 Oct 2023 21:00	2.7	NEN
23 Oct 2023 22:00	2.7	NEN	24 Oct 2023 22:00	2.7	NEN
23 Oct 2023 23:00	2.7	NEN	24 Oct 2023 23:00	2.7	NE

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
25 Oct 2023 00:00	2.7	NE	26 Oct 2023 00:00	2.7	E
25 Oct 2023 01:00	2.7	NEN	26 Oct 2023 01:00	2.7	NEE
25 Oct 2023 02:00	2.6	NEN	26 Oct 2023 02:00	2.7	NEE
25 Oct 2023 03:00	2.7	NEN	26 Oct 2023 03:00	2.7	N
25 Oct 2023 04:00	2.7	N	26 Oct 2023 04:00	2.7	NEN
25 Oct 2023 05:00	2.6	NE	26 Oct 2023 05:00	2.7	N
25 Oct 2023 06:00	2.7	NEN	26 Oct 2023 06:00	2.7	NEN
25 Oct 2023 07:00	2.7	NE	26 Oct 2023 07:00	2.6	N
25 Oct 2023 08:00	2.7	NEE	26 Oct 2023 08:00	2.7	NEN
25 Oct 2023 09:00	2.7	NEE	26 Oct 2023 09:00	2.7	NE
25 Oct 2023 10:00	2.7	NEN	26 Oct 2023 10:00	2.6	NEE
25 Oct 2023 11:00	2.7	N	26 Oct 2023 11:00	2.6	NE
25 Oct 2023 12:00	2.7	NEE	26 Oct 2023 12:00	2.7	NEE
25 Oct 2023 13:00	2.7	SWW	26 Oct 2023 13:00	2.7	NEE
25 Oct 2023 14:00	2.6	SEE	26 Oct 2023 14:00	2.7	SE
25 Oct 2023 15:00	2.7	NEE	26 Oct 2023 15:00	2.7	NEN
25 Oct 2023 16:00	2.7	N	26 Oct 2023 16:00	2.7	N
25 Oct 2023 17:00	2.7	N	26 Oct 2023 17:00	2.7	NEN
25 Oct 2023 18:00	2.7	N	26 Oct 2023 18:00	2.7	N
25 Oct 2023 19:00	2.7	N	26 Oct 2023 19:00	2.7	NEN
25 Oct 2023 20:00	2.7	NE	26 Oct 2023 20:00	2.7	NEN
25 Oct 2023 21:00	2.7	NE	26 Oct 2023 21:00	2.7	NEN
25 Oct 2023 22:00	2.7	NE	26 Oct 2023 22:00	2.7	NEN
25 Oct 2023 23:00	2.6	E	26 Oct 2023 23:00	2.7	NEN

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
27 Oct 2023 00:00	2.6	NE	28 Oct 2023 00:00	2.7	NEN
27 Oct 2023 01:00	2.7	N	28 Oct 2023 01:00	2.7	N
27 Oct 2023 02:00	2.6	E	28 Oct 2023 02:00	2.7	N
27 Oct 2023 03:00	2.7	SEE	28 Oct 2023 03:00	2.8	N
27 Oct 2023 04:00	2.7	SE	28 Oct 2023 04:00	2.9	NEN
27 Oct 2023 05:00	2.7	SES	28 Oct 2023 05:00	3.0	N
27 Oct 2023 06:00	2.6	SEE	28 Oct 2023 06:00	2.7	NEN
27 Oct 2023 07:00	2.7	NEN	28 Oct 2023 07:00	2.6	NE
27 Oct 2023 08:00	2.7	NEN	28 Oct 2023 08:00	2.7	E
27 Oct 2023 09:00	2.7	SE	28 Oct 2023 09:00	2.8	NE
27 Oct 2023 10:00	2.7	NEN	28 Oct 2023 10:00	2.7	SES
27 Oct 2023 11:00	2.7	SWS	28 Oct 2023 11:00	2.7	SEE
27 Oct 2023 12:00	2.7	NE	28 Oct 2023 12:00	3.4	NE
27 Oct 2023 13:00	2.7	N	28 Oct 2023 13:00	3.6	NEN
27 Oct 2023 14:00	5.8	N	28 Oct 2023 14:00	3.0	NEN
27 Oct 2023 15:00	10.4	N	28 Oct 2023 15:00	3.3	N
27 Oct 2023 16:00	5.8	NEN	28 Oct 2023 16:00	3.5	NEN
27 Oct 2023 17:00	6.2	N	28 Oct 2023 17:00	3.0	N
27 Oct 2023 18:00	3.8	N	28 Oct 2023 18:00	2.7	N
27 Oct 2023 19:00	3.1	N	28 Oct 2023 19:00	4.8	N
27 Oct 2023 20:00	2.6	NEN	28 Oct 2023 20:00	3.2	NEN
27 Oct 2023 21:00	2.9	NEN	28 Oct 2023 21:00	3.1	N
27 Oct 2023 22:00	3.4	N	28 Oct 2023 22:00	4.1	NEN
27 Oct 2023 23:00	5.9	NEN	28 Oct 2023 23:00	2.9	N

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction	Date & Time	Wind Speed (m/s)	Wind Direction
29 Oct 2023 00:00	3.8	N	30 Oct 2023 00:00	2.7	N
29 Oct 2023 01:00	4.6	N	30 Oct 2023 01:00	3.0	NEN
29 Oct 2023 02:00	3.6	NEN	30 Oct 2023 02:00	2.8	NEN
29 Oct 2023 03:00	2.9	N	30 Oct 2023 03:00	2.7	NE
29 Oct 2023 04:00	2.9	NE	30 Oct 2023 04:00	2.7	E
29 Oct 2023 05:00	2.7	NEE	30 Oct 2023 05:00	2.7	NEN
29 Oct 2023 06:00	3.0	NEN	30 Oct 2023 06:00	2.7	NEN
29 Oct 2023 07:00	3.2	NE	30 Oct 2023 07:00	2.7	NE
29 Oct 2023 08:00	2.9	NE	30 Oct 2023 08:00	2.7	NEE
29 Oct 2023 09:00	2.9	N	30 Oct 2023 09:00	2.7	N
29 Oct 2023 10:00	8.0	NEN	30 Oct 2023 10:00	2.8	SE
29 Oct 2023 11:00	3.8	NE	30 Oct 2023 11:00	2.7	SEE
29 Oct 2023 12:00	3.0	NEE	30 Oct 2023 12:00	2.6	NE
29 Oct 2023 13:00	2.9	NEE	30 Oct 2023 13:00	2.6	SES
29 Oct 2023 14:00	2.7	NEN	30 Oct 2023 14:00	2.7	SEE
29 Oct 2023 15:00	4.3	NE	30 Oct 2023 15:00	2.7	SEE
29 Oct 2023 16:00	2.7	N	30 Oct 2023 16:00	2.7	NEE
29 Oct 2023 17:00	4.0	N	30 Oct 2023 17:00	2.7	NE
29 Oct 2023 18:00	3.5	NEN	30 Oct 2023 18:00	2.7	NEN
29 Oct 2023 19:00	3.9	N	30 Oct 2023 19:00	2.7	N
29 Oct 2023 20:00	3.0	NEE	30 Oct 2023 20:00	2.7	NEN
29 Oct 2023 21:00	3.0	N	30 Oct 2023 21:00	3.1	N
29 Oct 2023 22:00	4.3	N	30 Oct 2023 22:00	3.0	N
29 Oct 2023 23:00	2.6	NEN	30 Oct 2023 23:00	3.0	NEN

Wind Data (October 2023)

Date & Time	Wind Speed (m/s)	Wind Direction
31 Oct 2023 00:00	3.2	N
31 Oct 2023 01:00	2.8	N
31 Oct 2023 02:00	2.7	N
31 Oct 2023 03:00	2.7	N
31 Oct 2023 04:00	2.7	NEE
31 Oct 2023 05:00	2.7	N
31 Oct 2023 06:00	2.7	NEN
31 Oct 2023 07:00	2.7	E
31 Oct 2023 08:00	2.6	NE
31 Oct 2023 09:00	2.7	E
31 Oct 2023 10:00	2.7	SEE
31 Oct 2023 11:00	2.6	SWS
31 Oct 2023 12:00	3.1	SEE
31 Oct 2023 13:00	3.3	NE
31 Oct 2023 14:00	4.2	N
31 Oct 2023 15:00	7.6	N
31 Oct 2023 16:00	3.3	N
31 Oct 2023 17:00	3.9	N
31 Oct 2023 18:00	2.7	N
31 Oct 2023 19:00	4.0	N
31 Oct 2023 20:00	3.0	N
31 Oct 2023 21:00	2.7	NE
31 Oct 2023 22:00	2.7	NE
31 Oct 2023 23:00	3.0	N

Appendix K

Summary of ET's Site Environmental
Audit in the Reporting Month

Summary of ET's Site Environmental Audit in the Reporting Month

Parameters	Date	Observations and Recommendations	Follow-up
Air Quality		NA	
Noise		NA	
Water Quality		NA	
Chemical and Waste Management		NA	
Landscape and Visual Impact		NA	
Permit / Licenses		NA	
Others		NA	

Appendix L

Waste Flow Table

Waste Flow Table (October 2023)

Monthly Ending	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated		Actual Quantities of Recyclables Generation			
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Chemical Waste	General Refuse	Felled Trees	Metals	Paper / Cardboard Packaging	Plastics
	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000m3)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)
2023 Jan	0.238	0.000	0.000	0.000	0.238	0.000	0.000	3.070	0.000	0.000	0.000	0.000
2023 Feb	1.358	0.000	0.000	0.000	1.358	0.000	0.000	10.520	0.000	0.000	0.000	0.000
2023 Mar	1.565	0.000	0.000	0.000	1.565	0.000	0.000	16.230	0.000	0.000	0.000	0.000
2023 Apr	0.337	0.000	0.000	0.000	0.337	0.000	0.000	5.240	0.000	0.000	0.000	0.000
2023 May	0.014	0.000	0.000	0.000	0.014	0.000	0.000	6.420	0.000	0.000	0.000	0.000
2023 Jun	0.021	0.000	0.000	0.000	0.021	0.000	0.000	15.390	0.000	0.000	0.000	0.000
2023 Jul	0.011	0.000	0.000	0.000	0.011	0.000	0.000	6.600	0.000	0.000	0.000	0.000
2023 Aug	0.089	0.000	0.000	0.000	0.089	0.000	0.000	20.770	0.000	0.000	0.000	0.000
2023 Sep	0.120	0.000	0.000	0.000	0.120	0.000	0.000	7.600	0.000	0.000	0.000	0.000
2023 Oct	0.079	0.000	0.000	0.000	0.079	0.000	0.000	0.000	0.000	0.000	0.000	0.000
2023 Nov												
2023 Dec												
Total	3.753	0.000	0.000	0.000	3.753	0.000	0.000	91.840	0.000	0.000	0.000	0.000

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.

Appendix M

Cumulative Statistics on Environmental
Complaints, Notifications of Summons and
Successful Prosecutions

Environmental Complaints Log

Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Outcome	Date of Reply

Cumulative Statistics on Complaints

Environmental Aspects	Cumulative No. Brought Forward	No. of Complaints This Month	Cumulative Project-to-Date
Air	0	0	0
Noise	0	0	0
Water	0	0	0
Waste	0	0	0
Total	0	0	0

Cumulative Statistics on Notification of Summons and Successful Prosecutions

Environmental Aspects	Cumulative No. Brought Forward	No. of Notification of Summons and Prosecutions This Month	Cumulative Project-to-Date
Air	0	0	0
Noise	0	0	0
Water	0	0	0
Waste	0	0	0
Total	0	0	0

Appendix N

Implementation Status of Environmental
Mitigation Measures (Construction Phase)

Implementation Status of Environmental Mitigation Measures (Construction Phase)

EIA Ref. (No.)	Environmental Protection Measures (Construction Phase) ⁽¹⁾	Location & (Implementation Agent)	Implementation Status
3.7.1.1 (A1)	A) Air Quality	All construction sites / construction phase / upon completion of all construction activities (Contractor)	
	Sufficient dust suppression measures as stipulated under the <i>Air Pollution Control (Construction Dust) Regulation</i> (Cap. 311R), as well as good site practices and good housekeeping of the site should be properly implemented in order to minimise the construction dust generated. These measures include the followings::		
	a) Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather;		Implemented
	b) Use of frequent watering for particularly dusty construction areas and areas close to ASRs;		Implemented
	c) Use of frequent watering or water sprinklers for major haul roads, material stockpiling areas and other dusty activities within the construction site;		Implemented
	d) Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering should be applied to aggregate fines;		Implemented
	e) Provide hoarding of not less than 2.4 m high from ground level along the site boundary except for site entrance or exit;		Implemented
	f) Open temporary stockpiles should be avoided or covered. Prevent placing dusty material storage piles near ASRs;		Implemented
	g) Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations;		Implemented
	h) Establishment and use of vehicle wheel and body washing facilities at the exit points of the site;		Implemented
	i) Imposition of speed controls for vehicles on unpaved site roads, 8 km/hr is the recommended limit;		Implemented
	j) Routing of vehicles and position of construction plant should be at the maximum possible distance from ASRs;		Implemented
	k) Avoid position of material stockpiling areas, major haul roads and dusty works within the construction site close to concerned ASRs; and		Implemented
	l) Avoid unnecessary exposed earth.		Implemented
3.7.1.2 (A2)	Guidelines stipulated in EPD's <i>Recommended Pollution Control Clauses for Construction Contracts</i> should be incorporated in the contract documents to abate dust impacts. The clauses include:	All construction sites / construction phase / upon completion of all construction activities (Contractor)	
	a) The contractor shall observe and comply with the <i>Air Pollution Control Ordinance</i> and its subsidiary regulations, particularly the <i>Air Pollution Control (Construction Dust) Regulation</i> .		Implemented
	b) The contractor shall undertake at all times to prevent dust nuisance as a result of the construction activities.		Implemented
	c) The contractor shall ensure that there will be adequate water supply / storage for dust suppression.		Implemented
	d) The contractor shall devise, arrange methods of working and carrying out the works in such a manner so as to minimise dust impacts on the surrounding environment, and shall provide experienced personnel with suitable training to ensure that these methods are implemented.		Implemented
	e) Before the commencement of any work, the contractor may require to submit the methods of working, plant, equipment and air pollution control system to be used on the site for the engineer inspection and approval.		Implemented
3.4.1.4 (A3)	<u>Control on fuel combustion from the use of PMEs</u>	All construction sites / construction phase / upon completion of all construction activities (Contractor)	
	a) Legal control on the types of fuel allowed for use and their sulphur contents in commercial and industrial processes should be observed.		Implemented
	b) Only approved or exempted non-road mobile machinery should be allowed to be used in construction sites.		Implemented
	c) All construction plants are required to use ultra-low-sulphur diesel (ULSD) (defined as diesel fuel containing not more than 0.005% sulphur by weight).		Implemented

Note:

(1) Detailed EIA report and EM&A Manual reference refer to the Appendix B of approved EM&A Manual.

N/A: Not Available, N/O: Not Observed.

Implementation Status of Environmental Mitigation Measures (Construction Phase)

EIA Ref. (No.)	Environmental Protection Measures (Construction Phase) ⁽¹⁾	Location & (Implementation Agent)	Implementation Status
	B) Noise		
4.8.1.2 (B1)	Good Site Practice	All construction sites / construction phase / upon completion of all construction activities (Contractor)	
	The site practices listed below should be followed during construction works:		
	a) Only well-maintained PME to be operated on site and should be serviced regularly during construction;		Implemented
	b) Silencers or mufflers on construction equipment should be utilised (if appropriate) and should be properly maintained during the construction;		N/A
	c) Mobile plant, if any, should be sited as far away from NSRs as possible;		Implemented
	d) Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;		Implemented
4.8.1.3 – 4.8.1.4 & Table 7 (B2)	e) Plant known to emit noise strongly in one direction should, wherever possible, be orientated to direct noise away from the nearby NSRs; and	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented
	f) Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities		Implemented
	Use of Quiet PME		
	The Contractors may adopt alternative quiet PME as long as it can be demonstrated that they would not result in construction noise impacts worse than those predicted in this EIA Report. Use of quiet plant should be made reference to the Powered Mechanical Equipment (PME) listed in the Technical Memorandum or the Quality Powered Mechanical Equipment (QPME) / other commonly used PME listed in Environmental Protection Department (EPD) web pages as far as possible which includes the Sound Power Level (SWLs) for specific quiet PME.		Implemented
	Use of Movable Noise Barriers/Acoustic Mats		
	Movable noise barriers that can be placed close to the construction equipment and moved along with the PME are effective for screening noise from NSRs. A typical design which has been used locally is a wooden framed barrier with a cantilevered upper portion of superficial density no less than 10 kg/m ² on a skid footing with internal sound absorptive lining. This measure is particularly effective for low level zone of NSRs. A longer cantilevered top cover would be required to achieve screening benefits at upper floors of NSRs. The Contractor shall be responsible for the design and actual position of the movable noise barriers with due consideration given to the position and size of the PME, and the requirement of intercepting the line-of-sight from the NSRs to the PME, as well as ensuring that the barriers should have no opening and gap. It is anticipated that properly designed noise barriers would achieve a 5 dB(A) reduction for mobile PME and a 10 dB(A) reduction for static PME. Acoustic mat with surface mass of not less than 7kg/m ² would be used for plant items such as piling, oscillator and a 10 dB(A) noise reduction is anticipated.		Implemented
4.8.1.7 (B4)	Scheduling of Noisy Activities to outside Examination Period of HKBTS	All construction sites / construction phase / upon completion of all construction activities (Contractor)	
	To minimise the construction noise impact on HKBTS, the use of piling (oscillator) in ELS and concurrent use of concrete lorry mixer with other PMEs in steel fixing and concreting of structure should be avoided during the examination period of HKBTS.		Implemented
	Contractor should keep close communication with the operator of HKBTS to obtain the updated schedule of examination at the time conducting of the relevant construction works.		Implemented

Note:

(1) Detailed EIA report and EM&A Manual reference refer to the Appendix B of approved EM&A Manual.

N/A: Not Available, N/O: Not Observed.

Implementation Status of Environmental Mitigation Measures (Construction Phase)

EIA Ref. (No.)	Environmental Protection Measures (Construction Phase) ⁽¹⁾	Location & (Implementation Agent)	Implementation Status
5.8.1.1 (C1)	<u>Construction Site Runoff</u> Proper site management measures should be implemented to control site runoff and drainage, and thereby prevent high sediment loadings from entering nearby watercourses. The contractor should follow the practices, and be responsible for the design, construction, operation and maintenance of all the mitigation measures as specified in ProPECC PN 1/94 “ <i>Construction Site Drainage</i> ”. The design of the mitigation measures should be submitted by the contractor to the engineer for approval. These mitigation measures should include the following practices: a) At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct storm water to silt removal facilities. b) Sand / silt removal facilities such as sand / silt traps and sediment basins should be provided to remove sand / silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt / sand traps should be 5 minutes under maximum flow conditions. c) All drainage facilities and erosion and sediment control structures should always be regularly inspected and maintained to ensure proper and efficient operation and particularly during rainstorms. Deposited silt and grit should be regularly removed, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times. d) Measures should be taken to minimise the ingress of site drainage into excavations. Water pumped out from foundation excavations should be discharged into storm drains via silt removal facilities. e) If surface excavation works cannot be avoided during the wet season (April to October), temporarily exposed slope / soil surfaces should be covered by a tarpaulin or other means, as far as practicable, and temporary access roads should be protected by crushed stone or gravel, as excavation proceeds. Interception channels should be provided (e.g. along the crest / edge of the excavation) to prevent storm runoff from washing across exposed soil surfaces. Arrangements should always be in place to ensure that adequate surface protection measures can be safely carried out well before the arrival of a rainstorm. Other measures that need to be implemented before, during and after rainstorms are summarised in ProPECC PN 1/94. f) All vehicles and plant should be cleaned before leaving a construction site. An adequately designed and sited wheel washing facility should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. g) Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms.	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented Implemented Implemented Implemented Implemented Implemented Implemented
5.8.1.2 – 5.8.1.3 (C2)	<u>General Construction Activities</u> a) Debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering any nearby water bodies and public drainage system. b) Stockpiles of cement and other construction materials should be kept covered when not being used. c) Oils and fuels should only be used and stored in designated areas, which have pollution prevention facilities. d) All fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. Rainwater in the bunds should be cleared after each rain event. Waste oils, fuels and solvents collected within the bund should be handled and treated as chemical waste.	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented Implemented Implemented Implemented
5.8.1.4 (C3)	<u>Sewage Effluent</u> Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to handle sewage from the workforce. A licensed contractor would be responsible for appropriate disposal of waste matter and maintenance of these facilities.	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented

Sai O Trunk Sewer Sewage Pumping Station

EIA Ref. (No.)	Environmental Protection Measures (Construction Phase) ⁽¹⁾	Location & (Implementation Agent)	Implementation Status
	C) Water Quality		
5.8.1.5 (C4)	<u>Construction Works in Close Proximity of Inland Waters</u>	All construction sites / construction phase / upon completion of all construction activities (Contractor)	N/A
	The practices outlined in ETWB TC (Works) No. 5/2005 “Protection of natural streams/rivers from adverse impacts arising from construction works” should be adopted where applicable to minimise the water quality impacts upon any natural streams or surface water systems.		

Note:
(1) Detailed EIA report and EM&A Manual reference refer to the Appendix B of approved EM&A Manual.
N/A: Not Available, N/O: Not Observed.

Implementation Status of Environmental Mitigation Measures (Construction Phase)

EIA Ref. (No.)	Environmental Protection Measures (Construction Phase) ⁽¹⁾	Location & (Implementation Agent)	Implementation Status
	D) Waste Management		
6.5.1.3 (D1)	Good Site Practices	All construction sites / construction phase / upon completion of all construction activities (Contractor)	
	Recommendations for good site practices during the construction phase include:		
	a) Nomination of approved personnel, such as a site manager, to be responsible for implementation of good site practices, arrangements for waste collection and effective disposal to an appropriate facility;		Implemented
	b) Training of site personnel in site cleanliness, concepts of waste reduction, reuse and recycling, proper waste management and chemical waste handling procedures;		Implemented
	c) Provision of sufficient waste reception / disposal points, and regular collection of waste;		Implemented
	d) Adoption of appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;		Implemented
	e) Provision of regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors;		Implemented
	f) Adoption of a recording system for the amount of wastes generated, recycled and disposed (including the disposal sites); and		Implemented
6.5.1.4 (D2)	g) Preparation of Waste Management Plan (WMP), as part of the Environmental Management Plan (EMP).	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented
	Waste Reduction Measures		
	Recommendations to achieve waste reduction are discussed as follow:		
	a) Segregate and store different types of construction related waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;		Implemented
	b) Provide separate labelled bins to segregate recyclable waste such as aluminium cans from other general refuse generated by the work force, and to encourage collection by individual collectors;		Implemented
	c) Recycle any unused chemicals or those with remaining functional capacity;		Implemented
	d) Maximise the use of reusable steel formwork to reduce the amount of C&D materials;		Implemented
	e) Adopt proper storage and site practices to minimise the potential for damage to, or contamination of construction materials;		Implemented
6.5.1.6–6.5.1.7 (D3)	f) Plan the delivery and stock of construction materials carefully to minimise the amount of waste generated; and	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented
	g) Minimise over ordering and wastage through careful planning during purchasing of construction materials.		Implemented
	Reducing and Reuse of C&D Materials		
	a) Careful design, planning together with good site management can reduce over-ordering and generation of C&D materials such as concrete, mortar and cement grouts. Formwork should be designed to minimise the use of standard wooden panels, so that high reuse levels can be achieved. Alternatives such as steel formwork or plastic facing should be considered to increase the potential for reuse.		Implemented
6.5.1.8 (D4)	b) To minimise off-site disposal of inert C&D material, the excavated inert materials with suitable characteristics / size should be reused on-site as fill material as far as practicable, such as for backfilling of the box culvert and drainage pipe works.	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented
	c) Prior to disposal of non-inert C&D materials, wood, steel and other metals should also be separated for reuse and / or recycle where practicable so as to minimise the quantity of waste to be disposed of to landfill.		Implemented
	Storage of C&D Materials		
	Suitable areas should be designated within the works site boundaries for temporary stockpiling of C&D material. Within stockpile areas, the following measures should be taken to control potential environmental impacts or nuisance:		
6.5.1.8 (D4)	a) cover material during heavy rainfall;	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented
	b) locate stockpiles to minimise potential visual impacts; and		Implemented
	c) minimise land intake of stockpile areas as far as possible.		Implemented

Sai O Trunk Sewer Sewage Pumping Station

EIA Ref. (No.)	Environmental Protection Measures (Construction Phase) ⁽¹⁾	Location & (Implementation Agent)	Implementation Status
	D) Waste Management		
6.5.1.9 (D5)	<u>Disposal of C&D Materials</u>	All construction sites / construction phase / upon completion of all construction activities (Contractor)	
	a) In order to monitor the disposal of C&D materials at the designated public fill reception facility and landfill and to control fly-tipping, a trip-ticket system should be included.		Implemented
	b) When disposing inert C&D materials at a public filling reception facility, the material shall only consist of soil, rock, concrete, brick, cement plaster / mortar, inert building debris, aggregates and asphalt. The material shall be free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered to be unsuitable by the Filling Supervisor.		Implemented
6.5.1.10 & 6.5.1.12 (D6)	<u>Chemical Wastes</u>	Construction and Operational Phase	
	a) If chemical waste is produced at the construction site / the SPS, the contractor would be required to register with the EPD as a Chemical Waste Producer.		Implemented
	b) Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately.		Implemented
	c) Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosives, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc.		Implemented
	d) The contractor shall use a licensed collector to transport and dispose of the chemical wastes at the CWTC or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.		Implemented
6.5.1.11 & Table 6.2 (D7)	<u>General Refuse</u>	All construction sites / construction phase / upon completion of all construction activities (Contractor)	
	a) General refuse should be stored in enclosed bins or compaction units separate from C&D materials and chemical wastes.		Implemented
	b) A reputable waste collector should be employed by the contractor to remove general refuse / screenings from the site on a regular basis to minimise odour, pest and litter impacts.		Implemented
	c) Clearly labelled recycling bins should be provided on site to encourage segregation and recycling of aluminium and plastic wastes, and wastepaper to reduce general refuse production.		Implemented
	d) The contractor should carry out an education programme for workers in avoiding, reducing, reusing and recycling of materials generation. Posters and leaflets advising on the use of the bins should also be provided in the site as reminders. The recyclable waste materials should then be collected by reliable waste recycling agents on a regular basis.		Implemented
	e) The collected general refuse will be disposed of at NENT landfill.		Implemented

Note:

(1) Detailed EIA report and EM&A Manual reference refer to the Appendix B of approved EM&A Manual.

N/A: Not Available, N/O: Not Observed.

Implementation Status of Environmental Mitigation Measures (Construction Phase)

EIA Ref. (No.)	Environmental Protection Measures (Construction Phase) ⁽¹⁾	Location & (Implementation Agent)	Implementation Status
	E) Landscape and Visual		
Table 10.9 (E1)	<u>CM1 – Preservation of Trees</u>	All construction sites / construction phase / upon completion of all construction activities (Contractor)	N/A
	Trees to be retained in accordance with DEVB TCW No. 4/2020 - Tree Preservation.		
Table 10.9 (E2)	<u>CM2 – Compensatory Tree Planting</u>	All construction sites / construction phase / upon completion of all construction activities (Contractor)	N/A
	Any trees to be felled under the Project shall be compensated in accordance with DEVB TCW No. 4/2020 - <i>Tree Preservation</i> .		
Table 10.9 (E3)	<u>CM3 – Control of Night-time Lighting Glare</u>	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented
	Any lighting provision of the construction works at night shall be carefully controlled to prevent light overspill to the nearby VSRs and into the sky.		
Table 10.9 (E4)	<u>CM4 – Erection of Decorative Screen Hoarding</u>	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented
	Decorative Hoarding, which is compatible with the surrounding settings, shall be erected during construction to minimise the potential landscape and visual impacts due to the construction works and activities.		
Table 10.9 (E5)	<u>CM5 – Management of Construction Activities and Facilities</u>	All construction sites / construction phase / upon completion of all construction activities (Contractor)	Implemented
	The facilities and activities at works sites and areas, which include site office, temporary storage areas, temporary works etc., shall be carefully managed and controlled on the height, deposition and arrangement to minimise any potential adverse landscape and visual impacts.		
Table 10.9 (E6)	<u>CM6 – Reinstatement of Temporarily Disturbed Landscape Areas</u>	All construction sites / construction phase / upon completion of all construction activities (Contractor)	N/A
	All hard and soft landscape areas disturbed temporarily during construction due to temporary excavations, temporary works sites and works areas shall be reinstated to equal or better quality, to the satisfaction of the relevant Government Departments.		

Note:

(1) Detailed EIA report and EM&A Manual reference refer to the Appendix B of approved EM&A Manual.

N/A: Not Available, N/O: Not Observed

Appendix O

Summary of Outstanding Issues and
Deficiencies in the Reporting Month

Summary of Outstanding Issues and Deficiencies in the Reporting Month

Environmental Aspects	Outstanding Issues	Deficiencies
Air Quality	N/A	Any items of deficiencies can be referred to Appendix K.
Noise	N/A	
Water Quality	N/A	
Chemical and Waste Management	N/A	
Landscape and Visual Impact	N/A	
Permit / Licenses	N/A	
Others	N/A	
