

Highways Department

**Agreement No. HMW
5/2009 (EP) Traffic
Improvements to Tuen
Mun Road Town Centre
Section**

Monthly Environmental
Monitoring and Audit
Report - April 2011

Final



Certified by Environmental Team Leader
Coleman Ng
Ove Arup & Partners Hong Kong Ltd



Verified by Independent Environmental Checker
David Yeung
ENVIRON HK Limited

Contents

	Page
Executive Summary	1
1 Environmental Status	3
1.1 Project Background	3
1.2 Construction Programmed	3
1.3 Work Undertaken During the Reporting Month	3
1.4 Project Area, Sensitive Receivers and Environmental Monitoring locations	4
1.5 Impact Monitoring Schedule	5
1.6 Status of Environmental Licensing and Permitting	5
1.7 Purpose of the Report	5
2 Implementation Status	8
2.1 Implementation Status of Mitigation Measures	8
2.2 Updated Implementation Schedule	8
3 Air Monitoring	9
3.1 Air Monitoring Requirements	9
3.2 Air Monitoring Methodology	10
3.3 Monitoring Results and Observations	11
4 Noise Monitoring	12
4.1 Noise Monitoring Requirements	12
4.2 Noise Monitoring Methodology	13
4.3 Monitoring Results and Observations	14
5 Landscape and Visual Monitoring	17
5.1 Landscape and Visual Monitoring Requirements	17
5.2 Audit Results	18
5.3 Implementation Status of Consultation Phase Landscape and Visual Mitigation Measures	19
5.4 Recommendations, Corrective Actions and Outstanding Issues	19
6 Waste Disposal	20
7 Environmental Performance	20
7.1 Environmental Site Inspection	20
7.2 Complaint Record	22
7.3 Notification of Summons and Successful Prosecution	24
7.4 Review of Reasons of Non-Compliance	24
8 Future Key Issues	24
8.1 Key Issues for the Coming Month	24
8.2 Environmental Monitoring Program for the Coming Month	24
9 Conclusions and Recommendations	25

9.1	Conclusions	25
9.2	Recommendations	25
10	Reference	25

Appendices

Appendix A

Construction Programme

Appendix B

Environmental Monitoring Programme in the Reporting Month

Appendix C

Implementation Schedule of Mitigation Measures

Appendix D

Calibration Certificates and Spreadsheets of Air Monitoring Equipments

Appendix E

Impact Air Monitoring Results

Appendix F

Wind Data

Appendix G

Calibration Certificates of Noise Monitoring Equipments

Appendix H

Impact Noise Monitoring Results

Appendix I

Landscape Summary Report

Appendix J

Monthly Summary Waste Flow Table

Appendix K

Environmental Monitoring Programme for Coming Month

Executive Summary

This is the ninth monthly Environmental Monitoring and Audit (EM&A) report prepared by Ove Arup & Partners Hong Kong Limited (Arup), the designated Environmental Team (ET), for the Project "Traffic Improvement to Tuen Mun Road Town Centre Section". This report presents the results of EM&A works conducted in the month of April 2011 (1 to 30 April 2011).

In the reporting month, the following activities took place for the Project:

Site clearance

Site hoarding construction;

Tree felling and transplanting;

Temporary footbridge construction;

Piling works;

Ground investigation; and

Underground utilities and drainage diversion.

Monitoring of 24-hour Total Suspended Particulates (TSP) and noise during non-restricted hours was performed and the results were checked and reviewed. Site audits were conducted on weekly basis. The implementation of the environmental mitigation measures, Event and Action Plans were checked.

Impact monitoring was carried out at 6 air quality sensitive receiver (SR) and 6 noise SRs during the reporting month.

Environmental Monitoring Works – Breaches of Action and Limit Levels

Air Quality

All measured 24-hour TSP concentrations in the reporting month were below the Action and Limit (AL) Levels.

Noise

Totally seven limit level exceedances for noise measurements during non-restricted hours were recorded in the reporting month. Based on the field observations, it was revealed that the exceedances were mainly caused by traffic noise along Tuen Mun Road. It was therefore concluded that the noise exceedance was not related to the construction activities. No further actions were applicable. Construction works were carried out during the restricted hours, the conditions stipulated in CNPs of related construction works were strictly followed by the Contractor.

One noise complaint, hence, one Action Level exceedance was recorded in the reporting month.

Construction works were carried out during the restricted hours, the conditions stipulated in CNPs of related construction works were strictly followed by the Contractor. No non-compliance was recorded.

Landscape and Visual Audit

In the reporting month, landscape and visual site audit in accordance with the requirements stipulated in the EIA report was conducted on 7 and 21 April 2011.

In the reporting month, total 478 trees were felled and the pruning of the transplanted trees was carried out in accordance with the Specification for Tree Protection and Transplanting Works in Landscape Plan. The updated statuses of the felled and transplanted trees during the reporting month are described in Section 5.

The implementation and maintenance of landscape and visual mitigation measures, listed in EIA report, were checked during the site audit. No substantial change of LR, LCA and VSR was noted. No non-compliance has been triggered during the reporting month.

Waste Disposal

Inert C&D materials with actual amount of 6,490.960 m³ were generated and disposed of at public fills at Tuen Mun Area 38 in the reporting month. 47.010 m³ general refuse were generated and disposed of at WENT landfill in the reporting month.

Environmental Licensing and Permitting

Permits or licenses granted to the Project included the Environmental Permit of the Project (EP-342/2009/B), Chemical Waste Producer Registration (5213-324-G3597-01) and Construction Waste Billing Account (7010350);

6 numbers of Construction Noise Permits and 2 numbers of Wastewater Discharge License under WPCO (WT00007251-2010 and WT00008195-2011).

Environmental Auditing

A total of 4 environmental site audits were conducted on a weekly basis in the reporting month. No non-conformance to the environmental requirements was identified during the reporting month.

Complaint Log

Two environmental complaints regarding the water quality and construction noise were recorded in the reporting month. After the investigations, it is concluded that both complaints were attributable to the Contract. The corresponding mitigation measure due to the complaint was recommended to carry out by the Contractor. Nevertheless, the Contractor was reminded to implement proper mitigation measure as stipulated in EM&A Manual to minimize any noise and water quality implication.

Notifications of Summons and Successful Prosecutions

No summonses or prosecution related to the environmental issues were made against the Project in the reporting month.

Reporting Changes

There were no reporting changes in the reporting month.

Future Key Issues

Construction noise is one of the key environmental issues. The implemented construction noise mitigation measures should also be maintained and improved as necessary. Especially in restricted hours, the conditions stipulated in CNPs should be strictly followed when the construction works were carried out during the restricted hours.

Construction dust is another key environmental issue. The implemented construction dust mitigation measures should also be maintained and improved as necessary. Furthermore, water quality impact is also key environmental issue. As rainy season has approached, special attention should be paid to avoid any muddy surface runoff from exposed soil surface during rainy days. The effective and efficiency mitigation measures should be strictly implemented and improved if necessary.

1 Environmental Status

1.1 Project Background

Ove Arup & Partners Hong Kong Limited (Arup) was appointed by Highways Department (HyD) as the Environmental Team (ET) for *Agreement No. CE22/2005 (HY) Supplementary Agreement 1 Traffic Improvements to Tuen Mun Road Town Centre Section* (the Project) under Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section. Environmental parameters including air quality, noise and landscape and visual are required for baseline monitoring prior to the commencement of the Project. The Project was commenced on August 2010 and to be completed on January 2014.

The Project involves widening the following sections of TMR from dual-two carriageway to dual-three carriageway:

- Wong Chu Road Section, (from Wong Chu Road Interchange to Tuen Hing Road);
- Tuen Mun Town Plaza Section, (from Yan Oi Town Square to Tuen Hing Road).

The Project is a designated project under Schedule 2 of the Environmental Impact Assessment (EIA) Ordinance (Cap. 499). Environmental Monitoring and Audit (EM&A) work is required in accordance with the conditions stipulated in the Environmental Permit (EP) (EP-342/2009/A) and the EM&A Manual of the Project.

1.2 Construction Programme

An up-to-date rolling construction programme is attached in **Appendix A**.

1.3 Work Undertaken During the Reporting Month

The major construction activities carried out by the Contractor in the reporting month are summarized in **Table 1.1**. Location of the works area is indicated in **Figure 1.1**. The structure of the project organisation in relation to the environmental management is shown in **Figure 1.2**. Contacts of key environmental staff of the Project and are shown in **Table 1.2**.

Table 1.1 Construction activities in the reporting month

Locations	Major Works Undertaken
All area	Site clearance, site hoarding construction, tree felling and transplanting, ground investigation, temporary footbridge construction; pilling works, underground utilities and drainage diversion

Figure 1.1 Site plan of the Project

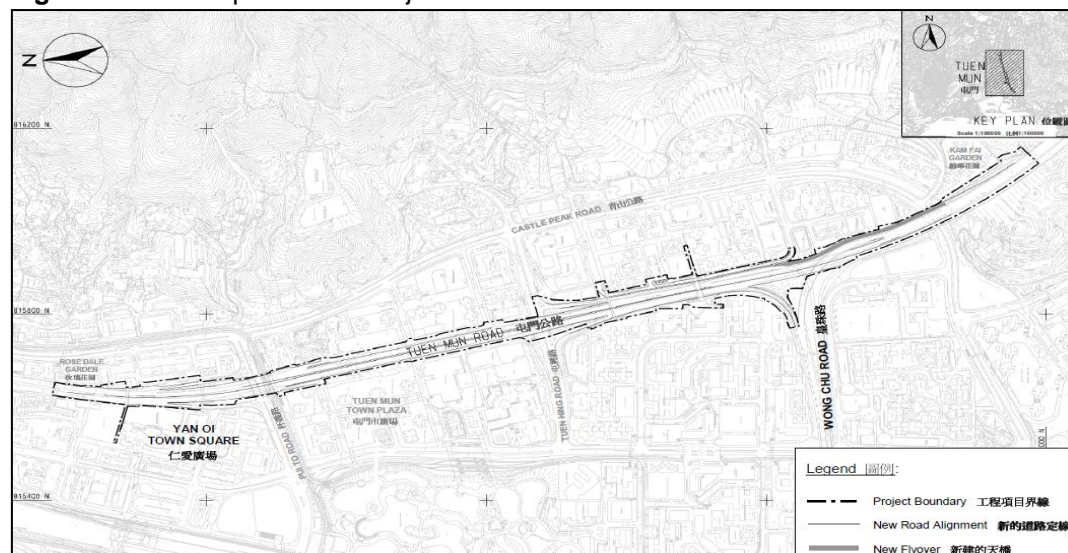
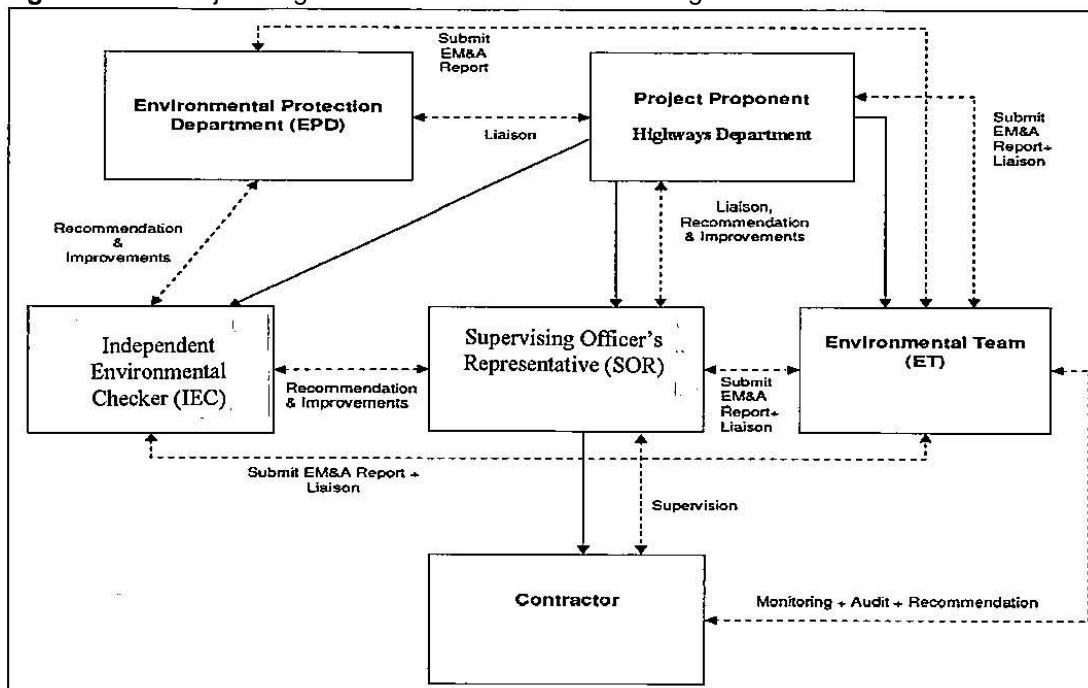


Figure 1.2 Project Organization – Environmental Management**Table 1.2** Contacts of key environmental staff

Organization	Name	Telephone
Environmental Protection Department		
Environmental Protection Officer (Strategic Assessment)22	Thomas To	2835 1103
Supervising Officer's Representative		
Highways Department: Senior Engineer	Kenneth Chan	2762 3422
Independent Environmental Checker		
ENVIRON Hong Kong Limited: Independent Environmental Checker	David Yeung	3743 0717
Environmental Team		
Ove Arup & Partners Hong Kong Ltd: Environmental Team Leader	Coleman Ng	2268 3097
Contractor		
China Harbour Engineering Company Limited		
Site Agent	W.S. Ng	2403 0529
Safety and Environmental Officer	Marko Chan	2403 0527

1.4 Project Area, Sensitive Receivers and Environmental Monitoring locations

The Project area is shown in **Figure 1.1**, while **Table 1.3** and **Figure 1.3** show the names and locations of the sensitive receivers and monitoring stations.

Table 1.3 Summary of air and noise monitoring stations

ID	Premise
Air	
AM1	Chung Sing Benevolent Society Mrs. Aw Boon Haw Secondary School
AM2	Tung Wah Group of Hospitals Tai Tung Pui Social Service Building
AM3	Shun Tak Fraternal Association Wu Siu Kui Memorial Primary School
AM4	The Chinese Manufacturers' Association Of Hong Kong Choi Cheung Kok Secondary School
AM5	Tuen Mun Town Hall

ID	Premise
AM6	Yan Oi Tong Jockey Club Community and Sports Centre
Noise	
N1	Kam Fai Garden
N2	Tung Wah Group of Hospitals Tai Tung Pui Social Service Building
N3	Po Leung Kuk The Hong Kong Taoist Association Yuen Yuen Primary School
N4	Shun Tak Fraternal Association Wu Siu Kui Memorial Primary School
N5	Tuen King Building
N6	The Chinese Manufacturers' Association Of Hong Kong Choi Cheung Kok Secondary School

1.5 Impact Monitoring Schedule

Environmental monitoring and audit will be carried out in accordance with the requirements stipulated in the EM&A manual. Air, noise, landscape and visual monitoring as well as weekly site audit schedule for the reporting month with respect to the construction programme is shown in **Appendix B**.

1.6 Status of Environmental Licensing and Permitting

All permits/licences inspected in the reporting month are summarised in **Table 1.4**. They are all properly kept by the contactor at their site office.


Table 1.4 Summary of environmental licensing status

Types of Permits / Licenses	Reference No.	Valid from	Valid to
Environmental Permit	EP-342/2009	15 May 09	Superseded
	EP-342/2009/A	27 Oct 09	Superseded
	EP-342/2009/B	14 Feb 11	N/A
Discharge License under WPCO	WT00007251-2010	12 Aug 10	31 Aug 15
	WT00008195-2011	06 Jan 11	30 Sep 15
Notification of Construction Work under APCO	Ref.: 314528	25 Feb 2010	N/A
Construction Noise Permit	GW-RW0589-10	24 Nov 10	21 May 11
	GW-RW0640-10	01 Dec 10	22 May 11
	PP-RW0022-10	23 Feb 11	31 May 11
	GW-RW0052-11	12 Feb 11	07 Aug 11
	GW-RW0164-11	12 Mar 11	12 Jun 11
	GW-RW0228-11	03 Apr 11	26 Jun 11
Chemical Waste Producer Registration	5213-424-C3597-01	26 Mar 10	N/A
Construction Waste Billing Account	7010350	25 Mar 10	N/A

1.7 Purpose of the Report

The purpose of the monthly EM&A report is to provide the information on monitoring methodology, monitoring results, environmental permit status, site audit findings, recommendations and conclusions for the scope of impact EM&A. This is the ninth monthly EM&A report summarising the monitoring methodology, locations, periods, frequencies, results and any observation from the air quality, noise, water quality, ecology, waste

management, landscape and visual monitoring and environmental site audit from 1 to 30 April 2011.

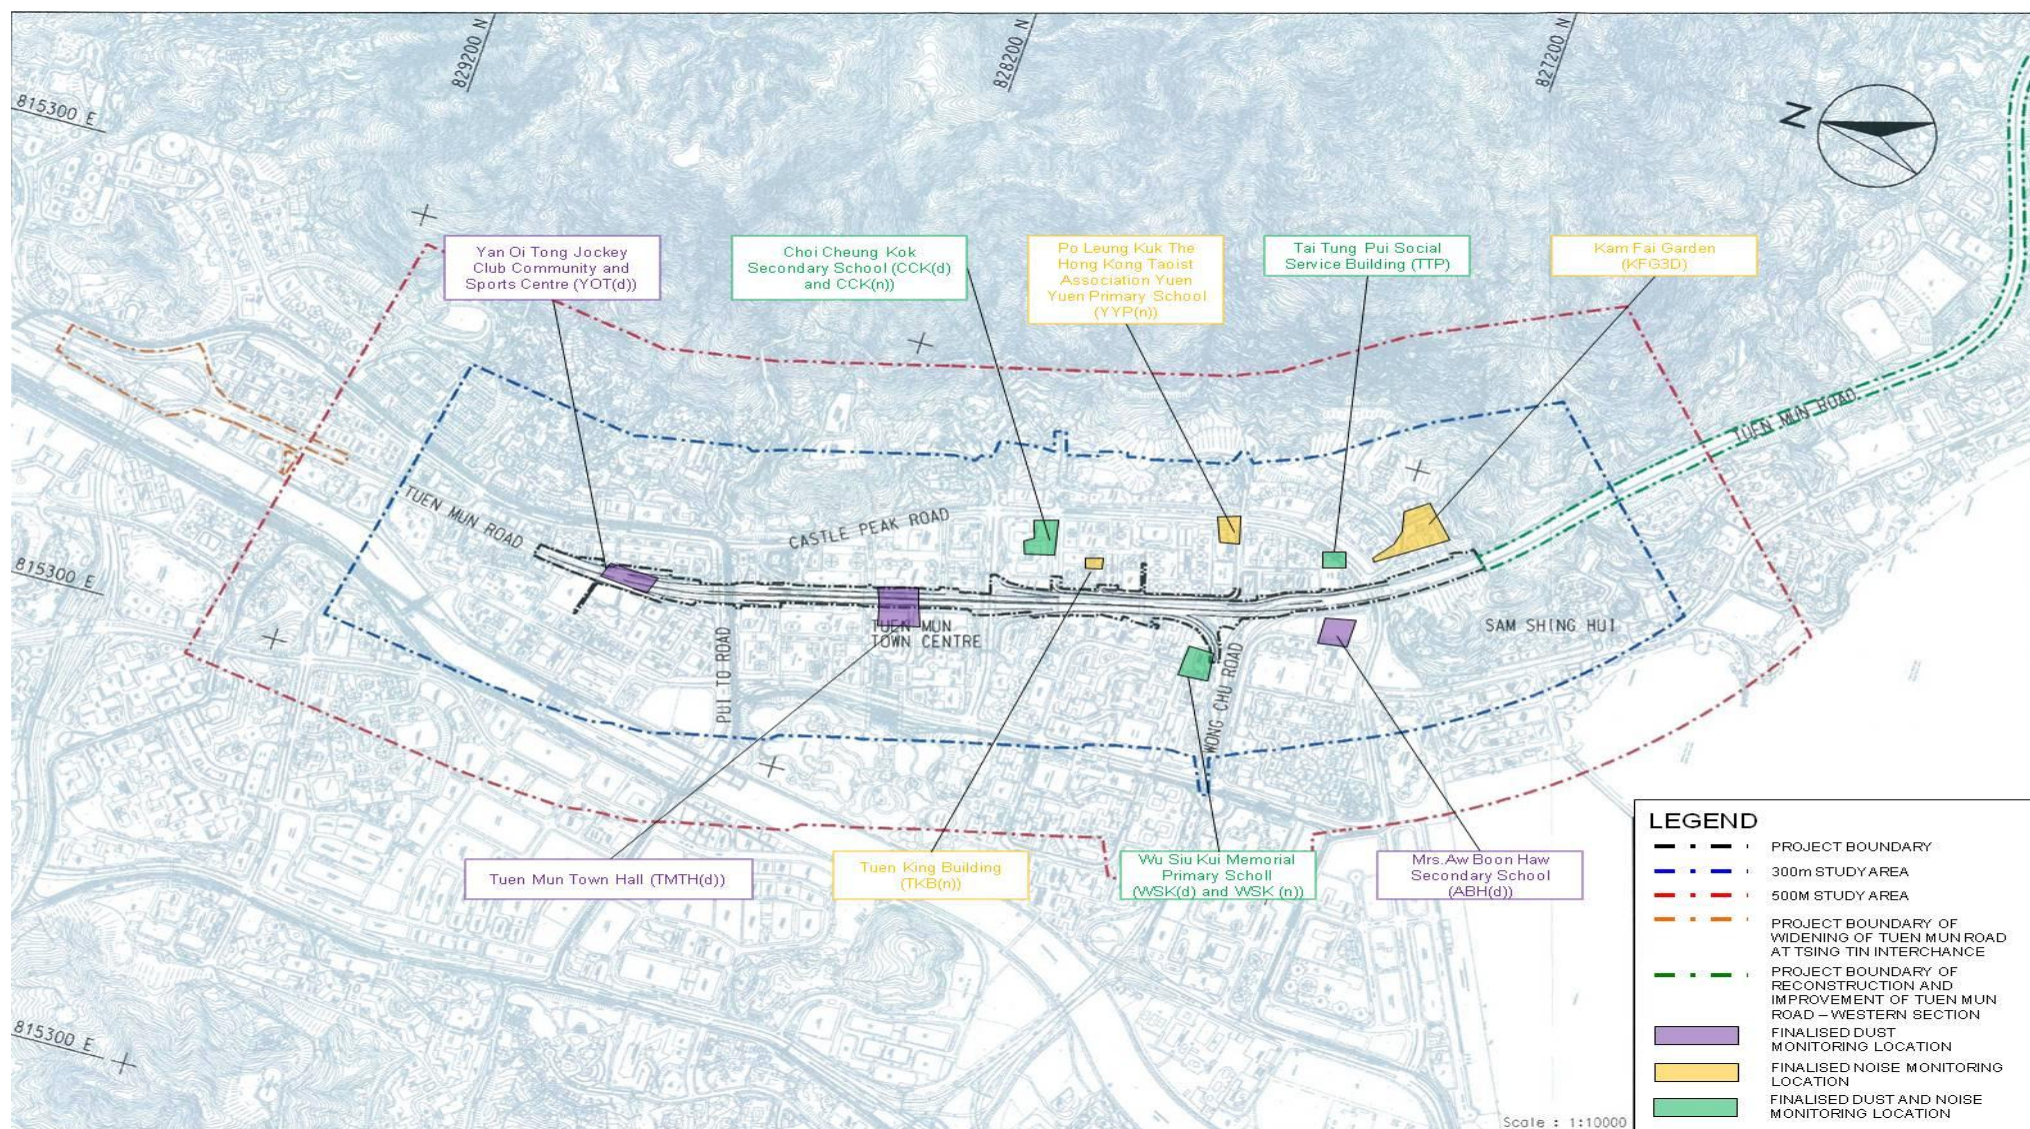Figure 1.3 Location of air and noise monitoring stations

2 Implementation Status

2.1 Implementation Status of Mitigation Measures

During weekly site inspections, the environmental protection, and pollution control/mitigation measures in accordance with the requirements stipulated in the EIA were observed. **Table 2.1** summarises the key observations and ET's corresponding recommendations while the Contractor's response and follow-up status are described in Section 7.1.

Table 2.1 Summary of the key observations and ET's recommendations

Location	Key Observations and Recommendations
Air Quality Mitigation Measures	
Yan Oi Tong Street, Tuen Hi Road	The Contractor was reminded to increase water spray frequency to minimise dust impact.
Water Quality Mitigation Measures	
Yan Ching Street, Tuen Hi Road	The contractor should provide adequate sandbags bunding along water barrier to avoid surface runoff overflowing to public area at both locations. Damaged sands along site boundary at Tuen Hi Road should be replaced as soon as possible.
Rose Garden	Accumulated debris and silt in the U-channel should be removed as soon as possible.
Yan Oi Tong Street	The contractor was reminded to liaise with SOR to ascertain the purpose of a section which currently without hoarding. If the section was used for site entrance/exit wheel washing facility should be provided. Hoarding should be provided otherwise
Yan Ching Street	The contractor was reminded to re-installed damaged fabric hoarding and seal gaps between fabrics.
Tsing Hoi Circuit	The contractor was reminded to follow approved/agreed drainage plan to avoid waste (including surface runoff) leaving the site without treatment.
Tuen Hi Road	The damaged sandbags along the site boundary should be replaced to avoid the sand dropping to public area.
Tsing Hoi Playground	The contractor should provide the bunding along site boundary (TMR side) to avoid any soil/rock dropping to TMR.
Noise Mitigation Measures	
Tsing Hoi Circuit	The contractor was reminded not to use hand-held breaker without noise label.
Yan Ching Street	The contractor was reminded to add noise blanket to avoid noise compliant from a nearby home for elderly.
Landscape and Visual	
Rose Garden and Yan Oi Tong Circuit	Fencing should be provided for the retained trees protection.
Waste Management	
Tuen Hi Road	The debris and construction waste should be removed regularly to avoid accumulation.
	The muddy surface between Tuen Mun Road and Tuen Hi Road should be cleaned.
Yan Ching Street	The contractor should remove the accumulated silt and mud outside the bunding area as well as the stagnant water as soon as possible.
Yan Oi Tong Street	The Contractor was reminded to conduct proper waste (metal, paper and plastic) segregation.

2.2 Updated Implementation Schedule

According to the Environmental Permit, the mitigation measures detailed in the permits are required to be implemented. The Implementation Schedule of Mitigation Measures was inspected during the weekly site inspections in reporting month. The details of the findings/observations are described in Section 7.1. An updated summary of the Implementation Schedule of Mitigation Measures is presented in **Appendix C**.

3 Air Monitoring

3.1 Air Monitoring Requirements

Monitoring Parameters

Air quality monitoring shall be measured in terms of the TSP levels for 1-hour and 24-hour period.

Monitoring Frequency

24-hour TSP levels shall be monitored during the construction stage while 1-hour TSP levels shall be required to monitor in case of complaints received. The monitoring parameters and frequency are summarised in **Table 3.1**.

Table 3.1 TSP monitoring parameters and frequency

Parameters	Monitoring Frequency
24-hour TSP	Once every 6 days
1-hour TSP	3 times every 6 days (as required in case of complaints)

Monitoring Locations

In accordance with the EM&A Manual and the subsequent Baseline Report, six air quality monitoring locations during construction stage are required, namely:

- (i) Chung Sing Benevolent Society Mrs. Aw Boon Haw Secondary School (AM1);
- (ii) Tung Wah Group of Hospitals Tai Tung Pui Social Service Building (AM2);
- (iii) Shun Tak Fraternal Association Wu Siu Kui Memorial Primary School (AM3);
- (iv) The Chinese Manufacturers' Association Of Hong Kong Choi Cheung Kok Secondary School (AM4);
- (v) Tuen Mun Town Hall (AM5); and
- (vi) Yan Oi Tong Jockey Club Community and Sports Centre (AM6).

Wind Monitoring

Wind monitoring data including wind speed and wind directions shall be collected from Hong Kong Observatory – Tuen Mun Monitoring Station.

Environmental /Quality Performance Limits

The monitoring results will be checked against the Action and Limit levels described in the Baseline Report, of which they are excerpted and summarised in **Tables 3.2 and 3.3**.

Table 3.2 Action and Limit Level for air quality monitoring of 1-hour TSP level

Level	Air Monitoring Stations					
	AM1	AM2	AM3	AM4	AM5	AM6
Action Level, $\mu\text{g}/\text{m}^3$	290	291	287	292	286	290
Limit Level, $\mu\text{g}/\text{m}^3$	500					

Notes:

1-hr TSP monitoring would be required in case of receiving complaints.

Table 3.3 Action and Limit Level for air quality monitoring of 24-hour TSP level

Level	Air Monitoring Stations (Note 1)					
	AM1	AM2	AM3	AM4	AM5	AM6
Action Level, $\mu\text{g}/\text{m}^3$	146	151	150	150	146	147
Limit Level, $\mu\text{g}/\text{m}^3$	260					

3.2 Air Monitoring Methodology

3.2.1 Monitoring Equipment

High Volume Sampler (HVS) was used to monitor the 24-hour TSP. **Table 3.4** shows the equipment used for the air quality monitoring.

Table 3.4 Air quality equipment list for impact air quality monitoring

Equipment	Manufacturer & Model No	Measurement Parameter	Quantity	Serial No.
High Volume Sampler	GS-2310105 / TE-5170	24-hour TSP	6	521, 522, 505, 1278, 516 & 510
Fibreglass Filter	G810		42	-
HVS Calibration Kit	GMW-2535		1	1378

3.2.2 Maintenance and Calibration

The HVSs and their accessories were frequently checked and maintained in accordance with the manufacturer's operation and maintenance manual. The maintenance included checking of supporting screen and gasket, as well as routine replacement of motor carbon brushes for the blower motor. The power cords and power supply were checked each time before sampling to ensure proper operation.

The HVSs were calibrated at 2-month intervals using GMW-2535 calibration kit which is re-calibrated by the manufacturer after one year of use. The calibration spreadsheets of the HVS and calibration certificate of the calibration kit are provided in **Appendix D**.

3.2.3 Monitoring Procedures

Specifications of the HVS are as follows:

- 0.6 – 1.7 m³/min (20 – 60SCFM);
- Equipped with a timing/control device with +/- 5 minutes accuracy for 24 hour operation;
- Installed with elapsed time meter with +/- 2 minutes accuracy for 24 hour operation;
- Capable of providing a minimum exposed area of 406 cm² (63in²);
- Flow control accuracy: +/-2.5% deviation over 24-hour sampling period;
- Equipped with a shelter to protect the filter and sampler;
- Incorporated with an electronic mass flow rate controller or other equivalent devices;
- Equipped with a flow recorder for continuous monitoring;
- Provided with a peaked roof inlet;
- Incorporated with a manometer;
- Able to hold and seal the filter paper to the sampler housing at horizontal position;
- Easy to change the filter; and
- Capable of operating continuously for 24-hour period.

The HVSs were equipped with an electronic mass flow controller and calibrated against a traceable standard at regular intervals. All equipment, calibration kit and filter papers were clearly labelled.

The relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and other special phenomena observed and work progress of the concerned site were recorded.

A HOKLAS accredited laboratory (ALS Technichem (HK) Pty Ltd (HOKLAS no.: 066)), in accordance with their standard QA/QC procedures, with constant temperature and humidity

control as well as equipped with necessary measuring and conditioning instruments to handle the 24-hour TSP samples was employed for sample analysis, and equipment calibration and maintenance. Filter papers of size 8"x10" were labelled before sampling. They were inspected clean with no pin holes and conditioned in a humidity controlled chamber for over 24-hour and be pre-weighed before use for the sampling.

The 24-hour TSP levels were measured by following the standard High Volume Method for Total Suspended Particulates as set out in the *Title 40 of the United States Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. TSP was sampled by drawing air through a conditioned, pre-weighed filter paper inside the HVS at a controlled air flow rate. After 24-hour sampling, the filter papers loaded with dust were kept in a clean and tightly sealed plastic bag, and then returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with a readout down to 0.1 mg. All the collected samples shall be kept in a good condition for 6 months before disposal.

3.3 Monitoring Results and Observations

3.3.1 Weather Condition

No adverse weather conditions were recorded during the monitoring dates.

3.3.2 Air Quality Monitoring Results

Monitoring of 24-hour TSP was conducted on 1, 6, 11, 16, 20, 26 and 30 April 2011. All monitoring data and graphical presentation of the monitoring results are provided in **Appendix E** and are summarised in **Table 3.5**. The graphical presentations of the monitoring results are provided in **Appendix E**. Wind data obtained from the Hong Kong Observatory – Tuen Mun station during the reporting period is presented in **Appendix F**.

Table 3.5 Summary of impact air quality monitoring results for reporting month

	Location					
	AM1	AM2	AM3	AM4	AM5	AM6
Average 24-hr TSP Concentration, $\mu\text{g}/\text{m}^3$ (Range)	59 (38 – 101)	53 (39 – 93)	67 (35 – 133)	53 (26 – 78)	58 (26 – 94)	54 (42 – 83)

All 24-hour TSP measurements during the reporting month were below the Action/Limit Level. No exceedance of action and limit level was found.

3.3.1 General Observations

Major construction works including site clearance, site hoarding construction, pilling works, ground investigation and underground utilities diversion were implemented during the reporting month. No abnormal condition was recorded during monitoring period.

4 Noise Monitoring

4.1 Noise Monitoring Requirements

Monitoring Parameters

Construction noise shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). L_{10} and L_{90} shall also be recorded as supplementary reference information for data auditing.

Monitoring Frequency

Noise measurements shall be conducted on a weekly basis. The monitoring time periods, monitoring parameters and frequency are summarised in **Table 4.1**.

Table 4.1 Construction noise monitoring parameters and frequency

Time Period (when construction activity is found)	Parameters	Monitoring Frequency
Between 0700-1900 hours on normal weekdays	$L_{eq}(30\text{ min})$	Once per week
Between 1900-2300 hours on normal weekdays	$L_{eq}(5\text{ min})^*$	
Between 2300-0700 hours of next day		
Between 0700-1900 hours on holidays		

* The $L_{eq(5 \text{ min})}$ will only be measured if construction activities are conducted.

Monitoring Location

In accordance with the EM&A Manual and the subsequent Baseline Report, six noise monitoring location during construction stage is required, namely:

- (i) Kam Fai Garden (N1);
- (ii) Tung Wah Group of Hospitals Tai Tung Pui Social Service Building (N2);
- (iii) Po Leung Kuk The Hong Kong Taoist Association Yuen Yuen Primary School (N3);
- (iv) Shun Tak Fraternal Association Wu Siu Kui Memorial Primary School (N4);
- (v) Tuen King Building (N5); and
- (vi) The Chinese Manufacturers' Association of Hong Kong Choi Cheung Kok Secondary School (N6).

Environmental /Quality Performance Limits

The monitoring results will be checked against the Action and Limit levels described in the Baseline Report, of which they are excerpted and summarised in **Tables 4.2**.

Table 4.2 Action and Limit Levels of construction noise

Location (Note 1)	Time Period	Action Level	Limit Level dB(A) (Note 2)
N1, N2 & N5	0700 - 1900 hours on normal weekdays	When one document ed complaint is received	75
	0700 - 2300 hours on holiday; and 1900 – 2300 hours on all other days		-
	2300 – 0700 hours of next day		-
N3, N4 & N6	0700 - 1900 hours on normal weekdays	When one document ed complaint is received	70/65 (Note 3)
	0700 - 2300 hours on holiday; and 1900 – 2300 hours on all other days		-
	2300 – 0700 hours of next day		-

Notes:

The detail of monitoring locations was presented in Table 2.2.

For normal day-time working hours, the noise criteria are 70 dB(A) and 65 dB(A) for normal reaching periods and examination period respectively.

If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be follows.

4.2 Noise Monitoring Methodology

4.2.1 Monitoring Equipment

Noise level was measured by a Sound Level Meter (SLM) in terms of A-weighted equivalent continuous sound pressure level. L_{eq} , L_{10} and L_{90} were recorded as supplementary information for data auditing. **Table 4.3** shows the equipment list of the noise monitoring.

Table 4.3 Noise equipment list for impact noise monitoring

Equipment	Manufacturer & Model No.	Serial No.	Precision Grade	Qty.
Integrated SLM	Brüel & Kjær 2238	2320694, 2320696, 2320707, 2562763, 2654435 & 2654436	IEC 651 Type 1 IEC 804 Type 1	6
½" free-field microphone	Brüel & Kjær 4188	2641132, 2630747, 2630746, 2658559, 2658546 & 2658547		6
Windshield	Brüel & Kjær UA0237	--		6
Sound level calibrator	Rion NC-74	34304660	IEC 942 Type 1	1

4.2.2 Maintenance and Calibration

The SLM and calibrator in compliance with the International Electrotechnical Commission (IEC) Publication 651:1979 (Type 1) and 804:1985 (Type 1) specifications according to the EM&A manual.

SLM complying with the standards of IEC 651 (Fast, Slow, Impulse rms detector tests) and IEC 804 (L_{eq} functions) and acoustical calibrator complying with IEC 942 were adopted for the noise measurement. All equipments are calibrated annually in-house using Brüel & Kjær (B&K) calibrator model no 4226. The 4226 calibrator is annually calibrated under the accreditation of United Kingdom Accreditation Service. The in-house calibration that has been undertaken can be traced back to the National Physical Laboratory. The calibration certificates for the noise equipment are given in **Appendix G**.

4.2.3 Monitoring Procedures

- The SLM and battery were checked to ensure that they are in proper condition. The SLM was set on a tripod at 1.2m above ground and at least 1m from the exterior of the building façade;
- Before conducting the measurement, the SLM was calibrated by an acoustical calibrator;
- Measurement parameter was set to A-weighted sound pressure level. The time weighting was set in fast response and the time period of measurement at 30 minutes;
- Wind speed was checked during noise monitoring to ensure the steady wind speed does not exceed 5m/s, or wind with gusts does not exceed 10m/s;
- Any abnormal conditions that generated intrusive noise during the measurement was recorded on the field record sheet;
- After each measurement, the equivalent continuous sound pressure level (L_{eq}), L_{10} and L_{90} were recorded on the field record sheet;
- After conducting the measurement, the SLM was calibrated by a sound level calibrator; and

- The SLM was re-calibrated by the sound level calibrator to confirm that there is no significant drift of reading. Measurements shall be accepted as valid only if the calibration levels before and after the noise measurement agrees to within 1.0 dB.

4.3 Monitoring Results and Observations

4.3.1 Weather Condition

The weather condition was mainly sunny during the noise monitoring period in the reporting month.

4.3.2 Noise Monitoring Results

Monitoring of the construction noise level was conducted during non-restricted hours on 2, 7, 12, 21 and 27 April 2011 at monitoring locations N1, N2, N3, N4, N5 and N6. All monitoring data and graphical presentation of the monitoring results are provided in **Appendix H** and are summarised in **Table 4.4 to 4.9**. The graphical presentations of the monitoring results are provided in **Appendix H**.

Table 4.4 Summary of impact noise monitoring at location N1 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level dB(A)
		Leq (30-min)	Leq (30-min)	Leq (30-min)	
2 Apr 11	09:50-10:20	77	76	72	75
7 Apr 11	09:45-10:15	73		Measured ≤ Baseline	
12 Apr 11	09:45-10:15	78		73	
21 Apr 11	09:45-10:15	75		Measured ≤ Baseline	
27 Apr 11	10:45-11:15	78		74	

Notes:

- Construction Noise Level = Measured Noise Level – Baseline Noise Level.

Table 4.5 Summary of impact noise monitoring at location N2 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level dB(A)
		Leq (30-min)	Leq (30-min)	Leq (30-min)	
2 Apr 11	10:10-10:40	77	78	Measured ≤ Baseline	75
7 Apr 11	10:30-11:00	73		Measured ≤ Baseline	
12 Apr 11	10:30-11:00	78		Measured ≤ Baseline	
21 Apr 11	10:30-11:00	76		Measured ≤ Baseline	
27 Apr 11	11:30-12:00	77		Measured ≤ Baseline	

Notes:

- Construction Noise Level = Measured Noise Level – Baseline Noise Level.

Table 4.6 Summary of impact noise monitoring at location N3 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level dB(A)
		Leq (30-min)	Leq (30-min)	Leq (30-min)	
2 Apr 11	11:20-11:50	66	69	Measured ≤ Baseline	70
7 Apr 11	11:15-11:45	66		Measured ≤ Baseline	
12 Apr 11	11:05-11:35	66		Measured ≤ Baseline	
21 Apr 11	11:05-11:35	68		Measured ≤ Baseline	

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level
		Leq (30-min)	Leq (30-min)	Leq (30-min)	dB(A)
27 Apr 11	13:00-13:30	69		Measured ≤ Baseline	

Notes:

1. Construction Noise Level = Measured Noise Level – Baseline Noise Level.

Table 4.7 Summary of impact noise monitoring at location N4 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level
		Leq (30-min)	Leq (30-min)	Leq (30-min)	dB(A)
2 Apr 11	08:30-09:00	66	67	Measured ≤ Baseline	70
7 Apr 11	08:30-09:00	65		Measured ≤ Baseline	
12 Apr 11	08:30-09:00	67		Measured ≤ Baseline	
21 Apr 11	08:30-09:00	67		Measured ≤ Baseline	
27 Apr 11	11:30-12:00	67		Measured ≤ Baseline	

Notes:

1. Construction Noise Level = Measured Noise Level – Baseline Noise Level.

Table 4.8 Summary of impact noise monitoring at location N5 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level
		Leq (30-min)	Leq (30-min)	Leq (30-min)	dB(A)
2 Apr 11	13:00-13:30	70	70	Measured ≤ Baseline	75
7 Apr 11	13:00-13:30	70		Measured ≤ Baseline	
12 Apr 11	13:00-13:30	71		62	
21 Apr 11	13:15-13:45	70		Measured ≤ Baseline	
27 Apr 11	13:50-14:20	72		66	

Notes:

1. Construction Noise Level = Measured Noise Level – Baseline Noise Level.

Table 4.9 Summary of impact noise monitoring at location N6 in the reporting month

Date	Time	Measured Noise Level, dB(A)	Baseline Noise Level, dB(A)	Construction Noise Level(Note1), dB(A)	Limit Level
		Leq (30-min)	Leq (30-min)	Leq (30-min)	dB(A)
2 Apr 11	14:00-14:30	68	69	Measured ≤ Baseline	70
7 Apr 11	13:50-14:20	70		59	
12 Apr 11	13:50-14:20	69		Measured ≤ Baseline	
21 Apr 11	14:00-14:30	69		Measured ≤ Baseline	
27 Apr 11	14:30-15:00	70		64	

Notes:

1. Construction Noise Level = Measured Noise Level – Baseline Noise Level.

Restricted Hours

In the reporting months, the construction works and activities such as mobilization of materials and plants etc were carried out during restricted hours. The granted Construction

Noise Permits (CNPs) were issued by EPD for the related activities before the works commencement, the Contractor strictly followed the conditions stipulated in the CNPs. There was no non-compliance recorded during the reporting month.

4.3.3 Exceedance of Limit and Action Levels for Construction Noise

Totally seven limit level exceedances for noise measurements during non-restricted hours were recorded in the reporting month, exceedances recorded on 2, 12 and 27 April 2011 at both locations N1 and N2, as well as 21 April 2011 for location N2. Based on the field observations, it was revealed that the exceedances were mainly caused by traffic noise along Tuen Mun Road. It was therefore concluded that the noise exceedance was not related to the construction activities. No further actions were applicable. Construction works were carried out during the restricted hours, the conditions stipulated in CNPs of related construction works were strictly followed by the Contractor. No Action Level exceedance was recorded in the reporting month.

Baseline noise level were retrieved and shown in **Table 4.4 to 4.9**. Comparison is made between the monitoring results against the baseline noise level, the monitoring results were lower to the baseline level. Based on the on-site observations and interpretation from the results, construction noise is considered insignificant and below the noise limits level. It is therefore concluded that the noise exceedance was not related to the construction activities. No further actions were applicable. It was however recommended that the Contractor shall maintain the existing practices stipulated in the EIA Report in order to minimise the potential noise impact in future.

One complaint regarding four complainants expressed that noise nuisance was generated during the restricted hours (night time and Sunday). The complaints were received by the ICC on 18 Apr (1 complaint from Chi Lok Fa Yuen), 21 Apr (1 complaint from Tuen Mun Fa Yuen) and 28 Apr 11 (2 complaints from Waldorf Garden and Tuen Mun Park Lane Square respectively) respectively. Therefore, one Action Level exceedance of construction noise was recorded in the reporting month.

Summary of above exceedance investigation of the Project is provided in the following Section 7.2 and **Appendix L**.

4.3.4 General Observations

The construction site had been under normal operation during the noise monitoring period and no unusual operation was observed. Traffic noise had been noticed at the monitoring location during the noise monitoring period.

5 Landscape and Visual Monitoring

5.1 Landscape and Visual Monitoring Requirements

Monitoring Parameters

The landscape and visual conditions of the site and its vicinity shall be reviewed with regards to parameters assessed in the EIA Report, including landscape resources (LR), landscape character area (LCA) and view condition of visual sensitive receiver (VSR).

Monitoring Frequency and Location

The landscape and visual monitoring and audit shall be undertaken bi-weekly throughout the construction period. The components of each assessed parameter of LR, LCA and VSR are summarised in **Table 5.1**.

Table 5.1 Parameters of landscape resources, landscape character areas and landscape sensitive receivers assessed during baseline site survey

ID No.	Names
Landscape Resources	
LR1	Tsing Sin Playground
LR2	Roadside Planting along Tuen Mun Road Adjacent to Kam Fai Garden
LR3	Street trees along Castle Peak Road – Castle Peak Bay
LR4	Street trees along Tuen Mun Road west of Chi Lok Fa Yuen and east of On Ting Estate
LR5	Street trees along Tuen Mun Road west of Waldorf Garden and CMA Choi Cheung Kok Prevocational School
LR6	Street trees along Tuen Mun Road near Tuen Mun Town Plaza
LR7	Street trees along Tuen Mun Road east of Yan Oi Tong
LR8	Trees at roadside planting areas near Yan Oi Tong Circuit
LR9	Trees at planting area near Tuen Mun Town Plaza
LR10	Trees at planting area near New Town Mansion
LR11	Trees at planting area near On Ting Estate
LR12	Tsing Hoi Playground
Landscape Character Areas	
LZ1	Tuen Mun Residential Urban Landscape
LZ2	Tuen Mun Mixed Modern Comprehensive Urban Development Landscape
LZ3	Tuen Mun 'Hui' Urban Landscape
Visual Sensitive Receivers	
C/R1	Tuen Mun Town Plaza, Waldorf Garden
C/R2	Tuen Cultural Centre, Tuen Mun Town Plaza
C/R3	Chelsea Height
GIC1	Tuen Mun Church and Tuen Mun Tseng Choi Street Joint-user Complex
GIC2	Sin Hing Tong Temple
GIC3	Sampe Memorial Secondary School and Chung Shing Benevolent Society Mrs. Aw Boon Haw Secondary School
GIC4	Car park (Open)
GIC5	Yan Oi Tong Community & Sports Centre
GIC6	Tuen Mun Government Secondary School, Choi Cheung Kok Secondary School

ID No.	Names
GIC7	Madam Lau Wong Fat Primary School, Lui Cheung Kwong College, Leung Kau Kui College, Lui Cheung Kwong Primary School, Wu Siu Kui Primary School
GIC8	Sam Shing Temple
O1	San Hui Playground
O2	Tsing Sin Playground
O3	Siu Lun Sports Ground
O4	Hoi Sin Playground
R1	Residential Area of Tuen Mun San Hui
R2	Residential Area along Yan Oi Tong Circuit
R3	On Ting Estate and Siu On Court
R4	Residential Area along Tsing Hoi Circuit
R5	Handsome Court, Alpine Garden, Hoi Tak Garden and Harvest Garden, Kam Fai Garden
R6	Siu Lun Court
R7	Goodview Garden and Tsui Ning Garden
R8	Sam Shing Estate
R9	Hanford Garden
T1	Tuen Mun Road – Vehicular and Pedestrian

5.2 Audit Results

In the reporting month, landscape and visual site audit in accordance with the requirements stipulated in the EIA report was conducted on 7 and 21 April 2011.

In accordance with the Landscape Plan of the Project under the Clause 2.13 of the Part C of the EP and updated information by the Contractor, a total of 1021 trees would be affected. 134 trees would be retained, 389 trees would be transplanted to Siu Lang Shui Road and 521 trees would be felled during the construction phase. The implementation and maintenance of landscape and mitigation measures, listed in EIA report, were checked during the site audit. No substantial change of LR, LCA and VSR was noted. No non-compliance has been triggered during the reporting month.

Since the commencement of the Project, total 478 trees were felled and the pruning of the transplanted trees was carried out in accordance with the Specification for Tree Protection and Transplanting Works in Landscape Plan. The updated statuses of the felled and transplanted trees during the reporting month are summarized in **Tale 5.2** and the summary report is presented in **Appendix I**.

Table 5.2 Status of felled and transplanted trees during reporting month

	No. of trees to be felled	No. of trees to be transplanted			
		Crown pruning	1 st root pruning	2 nd root pruning	3 rd root pruning
In progress	43	37	46	71	84
Completed	478	352	343	318	305
Total	521	389	389	389	389
Percentage completed (%)	92	90	88	82	78

In order to enhance the landscape and visual experience to Tuen Mun town centre neighborhood and compensate for the district tree felling, compensatory tree planting of 699 no. of trees would be carried out throughout various area in Tuen Mun after the discussion and agreement with Tuen Mun District Council (TMDC) and relevant government parties (e.g. LCSD).

5.3 Implementation Status of Consultation Phase Landscape and Visual Mitigation Measures

The design, implementation and maintenance of landscape and visual mitigation measures stipulated in the EM&A manual, were checked during the site audits. No non-compliance has been triggered.

The Implementation Schedule of Mitigation Measures was inspected during the weekly site inspections in reporting month. The details of the findings/observations are described in Section 7.1. Summary of the implementation status of construction phase Landscape and Visual mitigation measures are presented in **Appendix C**.

5.4 Recommendations, Corrective Actions and Outstanding Issues

The recommendations, corrective actions or outstanding issues in relation with the landscape and visual monitoring are as follows:

- The Contractor was reminded to strip and store the topsoil for re-use in the construction of soft landscape works, where practical;
- The Contractor was reminded to protect the retained trees carefully during construction;
- The Contractor was reminded to transplant the trees which affected by the works where possible and practical;
- The Contractor was reminded to compensate the trees for felled trees;
- The Contractor was reminded to control of night-time lighting;
- The Contractor was reminded to erect a compatible decorative screen hoarding with the surrounding setting;
- The Contractor was reminded to avoid placing the construction materials too close to the trees.

6 Waste Disposal

The actual amounts of different types of waste generated by the activities of the Project during the reporting month are shown in Table 6.1. The monthly summary flow table is provided in **Appendix J**.

Table 6.1 Amount of waste generated in reporting month

Waste Type	Amount	Disposal Locations
Inert C&D Materials	0 m ³	Broken concrete
	0 m ³	Reused in the Contract
	0 m ³	Reused in other Projects
	6,490.960 m ³	Disposal of at public fill at Tuen Mun Area 38
Chemical Waste	0 kg	N/A
Paper / cardboard packaging	0 kg	Recycler
Plastic	0 kg	
Metal	2,720.00 kg	
General Refuse	47.010 m ³	Disposal of at WENT landfill

7 Environmental Performance

7.1 Environmental Site Inspection

Environmental site inspections were carried out on a weekly basis to monitor environmental issues on the construction sites to ensure that all mitigation measures were implemented timely and properly. A summary of the site inspections in the reporting month is presented in **Table 7.1**.

Table 7.1 Key findings of weekly environmental site audit in the reporting month

Location	Inspection Date	Key Observations and Recommendations	Contractor's Response / Environmental Outcome	Closed Date / Follow up Status
Air Quality Mitigation Measures				
Yan Oi Tong Street, Tuen Hi Road	20 Apr 11	The Contractor was reminded to increase water spray frequency to minimise dust impact.	Agreed with the ET's advice.	Contractor had been noted. Closed on 28 Apr 11.
Water Quality Mitigation Measures				
Yan Ching Street, Tuen Hi Road	14 Apr 11	The contractor should provide adequate sandbags bunding along water barrier to avoid surface runoff overflowing to public area at both locations. Damaged sands along site boundary at Tuen Hi Road should be replaced as soon as possible.	Agreed with the ET's advice.	Sandbags bunding had been provided. Closed on 20 Apr 11.
Rose Garden	14 Apr 11	Accumulated debris and silt in the U-channel should be removed as soon as possible.	Agreed with the ET's advice.	Debris had been removed. Closed on 20 Apr 11.
Yan Oi Tong Street	20 Apr 11	The contractor was reminded to liaise with SOR to ascertain the purpose of a section which currently without hoarding. If the section was used for	Agreed with the ET's advice.	Contractor had been noted. Closed on 28 Apr 11.

Location	Inspection Date	Key Observations and Recommendations	Contractor's Response / Environmental Outcome	Closed Date / Follow up Status
		site entrance/exit wheel washing facility should be provided. Hoarding should be provided otherwise		
Yan Ching Street	20 Apr 11	The contractor was reminded to re-installed damaged fabric hoarding and seal gaps between fabrics.	Agreed with the ET's advice.	Contractor had been noted. Closed on 28 Apr 11.
Tsing Hoi Circuit	20 Apr 11	The contractor was reminded to follow approved/agreed drainage plan to avoid waste (including surface runoff) leaving the site without treatment.	Agreed with the ET's advice.	Contractor had been noted. Closed on 28 Apr 11.
Tuen Hi Road	28 Apr 11	The damaged sandbags along the site boundary should be replaced to avoid the sand dropping to public area.	Agreed with the ET's advice.	Damaged sandbags had been replaced. Closed on 5 May 11.
Tsing Hoi Playground	28 Apr 11	The contractor should provide the bunding along site boundary (TMR side) to avoid any soil/rock dropping to TMR.	Agreed with the ET's advice.	Bunding had been provided. Closed on 5 May 11.
Noise Mitigation Measures				
Tsing Hoi Circuit	20 Apr 11	The contractor was reminded not to use hand-held breaker without noise label.	Agreed with the ET's advice.	Contractor had been noted. Closed on 28 Apr 11.
Yan Ching Street	20 Apr 11	The contractor was reminded to add noise blanket to avoid noise compliant from a nearby home for elderly.	Agreed with the ET's advice.	Contractor had been noted. Closed on 28 Apr 11.
Landscape and Visual				
Rose Garden	14 Apr 11	Fencing should be provided for the retained trees protection.	Agreed with the ET's advice.	Fencing had been provided. Closed on 20 Apr and 5 May 11 respectively.
Yan Oi Tong Circuit	28 Apr 11			
Waste Management				
Tuen Hi Road	7 Apr 11	The debris and construction waste should be removed regularly to avoid accumulation.	Agreed with the ET's advice.	Debris and construction waste had been removed. Closed on 14 Apr 11.
Tuen Hi Road	7 Apr 11	The muddy surface between Tuen Mun Road and Tuen Hi Road should be cleaned.	Agreed with the ET's advice.	Muddy surface had been cleaned. Closed on 14 Apr 11.
Yan Ching Street	7 Apr 11	The contractor should remove the accumulated silt and mud outside the bunding area as well as the stagnant water as soon as possible.	Agreed with the ET's advice.	Accumulated silt and mud as well as stagnant water had been removed.

Location	Inspection Date	Key Observations and Recommendations	Contractor's Response / Environmental Outcome	Closed Date / Follow up Status
				Closed on 14 Apr 11.
Yan Oi Tong Street	20 Apr 11	The Contractor was reminded to conduct proper waste (metal, paper and plastic) segregation.	Agreed with the ET's advice.	Contractor had been noted. Closed on 28 Apr 11.

7.2 Complaint Record

Two environmental complaints regarding the water quality and construction noise were recorded in the reporting month.

The **first** complaint regarding three complainants expressed that muddy water spillage from the construction site in the vicinity of Tuen Mun Town Plaza (near Tuen Hi Road) was observed.

Three complaints regarding same issue were received by the ICC on 1, 3 and 4 Apr 11 respectively. ET received the complaints on 4 Apr 11.

As confirmed by the Contractor and Supervising Officer's Representative, muddy water was overflowed to Tuen Mun Road (Yuen Long bound) in the vicinity of Tuen Mun Town Plaza (near Tuen Hi Road) on 1 Apr 11 evening time.

Based on the information provided by the Contractor and Supervising Officer's Representative, the overflow of muddy spillage was anticipated to be from the broken hose to direct the pump to the wastewater treatment facility. Immediate actions were taken by the Contractor for ceasing the pump and cleaning of muddy spillage. It is therefore concluded that the complaint was work-related under the Project.

The site inspection was carried on 7 and 14 Apr 11, the damaged hose had been replaced and the condition was satisfactory. No abnormal operation was observed.

Nevertheless, it is recommended that the Contractor should undertake following mitigation measures to minimize the noise nuisance.

1. Inspect the conditions of the hoses and connections daily;
2. Well-maintain the hoses and connections condition and replace the old/damaged hoses and connections if necessary;
3. Relocate the hoses as far as possible from the machines and construction materials to minimize the possibility of damage;
4. Stock the spare pumps, hoses and connections on-site for immediate action in case of spillage occurs;
5. Provide adequate bunding along the site boundary to minimize the possibility of the muddy water overflowing to public area in case of spillage occurs; and
6. Enhance the workers awareness by regular training to handle the muddy water spillage incident.

The **second** complaint regarding four complainants expressed that noise nuisance was generated during the restricted hours (night time and Sunday) in the vicinity of Chi Lok Fa Yuen, Tuen Mun Garden, Waldort Garden and Park Lane Plaza.

Four complaints regarding same issue were received by the ICC on 18 Apr (1 complaint from Chi Lok Fa Yuen), 21 Apr (1 complaint from Tuen Mun Fa Yuen) and 28 Apr 11 (2

complaints from Waldorf Garden and Tuen Mun Park Lane Square respectively) respectively. ET received the complaints on 4 May 11.

As confirmed by the Contractor and Supervising Officer's Representative, the loading and unloading works at central median was carried out on TMR during the complaint period in the vicinity of Chi Lok Fa Yuen, Tuen Mun Garden, Waldorf Garden and Park Lane Plaza.

Totally 3 units of power mechanical equipments had been used including lorry, dump truck and excavator. The relevant construction noise permit (CNP) no. GW-RW0640-10 was obtained for the above works prior commencement. The conditions stipulated in the CNP were strictly followed by the Contractor. EPD had been informed prior the work commencement.

Based on the above-mentioned information provided by the Contractor, it is anticipated that the noise nuisance was mainly due to the machines operation. Therefore, it is concluded that the complaint was work-related under the Project.

In accordance with the Action/Event Plan, additional noise monitoring during the restricted hours was undertaken on 6 May 11 at the monitoring location N5 (Tuen King Building) and N6 (The Chinese Manufacturers' Association of Hong Kong Choi Cheung Kok Secondary School), where the loading and unloading works was carried out on TMR during restricted hours (night time) in the vicinity of these two monitoring locations.

Comparison is made between the monitoring results against the corresponding baseline noise level. Based on the interpretation from the results, the construction noise at both locations is 54dB(A) which below the night time noise limit level (55dB(A)).

Nevertheless, ET recommended that the Contractor should undertake following mitigation measures to minimize the noise nuisance.

1. Minimize the no. of machines used for the work as far as possible;
2. Well-maintain the machines condition to minimize noise nuisance;
3. Relocate operating machinery as far as possible from nearby sensitive receivers;
4. Machines that may be in intermittent use should be shut down between work periods or should be throttled down;
5. Optimize the working programme to minimize the restricted hours work activities as far as possible;
6. Improve the working practices to minimize the noise nuisance during the working activities as far as possible;
7. Provide temporary / mobile noise barrier for the noisy activities as far as possible; and
8. Enhance the workers awareness by regular training to minimize noise nuisance during the restricted hours.

The updated statistical summary of complaint is presented in **Table 7.2**. The updated complaint log (C003 and C004) of the Project in the reporting month is shown in **Appendix L**.

Table 7.2 Summary of complaints for the contract

Reporting Period	Complaint Statistics		Area of Concern	Validity to the Project	Status
	Number	Cumulative			
02/08/10 – 31/10/10	0	0	-	-	-
01/11/10 – 30/11/10	1	1	Noise	Yes (Ref.: C001)	Closed on 30 Nov 10.
01/12/10 – 31/01/11	0	1	-	-	-

Reporting Period	Complaint Statistics		Area of Concern	Validity to the Project	Status
	Number	Cumulative			
01/02/11 – 28/02/11	1	2	Noise	Yes (Ref.: C002)	Closed on 2 Mar 11.
01/03/11 – 31/03/11	0	2	-	-	-
01/04/11 – 30/04/11	2	4	Water	Yes (Ref.: C003)	Closed on 16 Apr 11.
			Noise	Yes (Ref.: C004)	Closed on 16 May 11.

7.3 Notification of Summons and Successful Prosecution

No summons or prosecutions related to environmental issues were received or made against the Project in the reporting month.

7.4 Review of Reasons of Non-Compliance

Seven limit level exceedances of noise monitoring were recorded from the monitoring data at locations N1 and N2, which triggered the Event and Action Plan for remedial action. Based on the on-site observations and interpretation from the results, it was revealed that the exceedances were mainly caused by traffic noise along Tuen Mun Road and was not related to the construction activities. No particular remedial work is required.

8 Future Key Issues

8.1 Key Issues for the Coming Month

Key issues to be considered in the coming month include:

- Dust generation from activities on-site, such as vehicular movements along unpaved area, excavation and demolition;
- Noise impact from operating equipment and machinery on-site;
- Muddy surface runoff overflow to public area;
- Uncontrolled water discharge into nearby water body;
- Storage and using of chemicals/fuel and chemical waste/waste oil on site;
- Disposal of construction waste; and
- Tree maintenance.

8.2 Environmental Monitoring Program for the Coming Month

Environmental monitoring and audit will be carried out in accordance with the requirements stipulated in the EM&A manual. Tentative air, noise, landscape and visual monitoring as well as weekly site audit schedule for the coming month with respect to the construction programme is shown in **Appendix K**.

The construction programme for the coming month is shown in **Table 8.1**.

Table 8.1 Tentative programme of construction works

Month	Locations	Details of Construction Works
May 2011	Various locations	Site clearance, site hoarding construction, tree transplanting, ground investigation, pilling works, temporary footbridge construction and underground utilities diversion

9 Conclusions and Recommendations

9.1 Conclusions

The construction phase of the Project was commenced on 2 August 2010. The EM&A programme has been implemented since then, including air quality, noise, landscape and visual and environmental site audits.

No Action and Limit Level exceedance was recorded for impact air quality in the reporting month.

Seven Limit level exceedances of noise monitoring were recorded from the monitoring data at locations N1 and N2, which triggered the Event and Action Plan for remedial action. Based on the on-site observations and interpretation from the results, noise exceedance was not related to the construction activities. No particular remedial work is required. But one noise complaint, hence one Action Level exceedance, was recorded in the reporting month.

Totally two environmental complaints regarding water quality and construction noise were recorded in the reporting month. After the investigation, it is concluded that both complaints were attributable to the Contractor. The corresponding mitigation measure due to the complaint was recommended to carry out by the Contractor.

No summons or prosecution related to environmental issues was received during the reporting month.

In accordance with the requirements stipulated in the EM&A manual, landscape and visual site audit was conducted on 7 and 21 April 2011. Total 478 trees were felled and the pruning of the transplanted trees was carried out during the reporting month. No substantial change of LR, LCA and VSR was noted.

Four (4) weekly environmental site audits were carried out during the reporting month. The major environmental concerns were related to air quality, noise, water quality, waste management and tree maintenance.

9.2 Recommendations

Impact monitoring will be continued to carry out in the following month and followed by the requirement stipulated in the EM&A manual. Attention will be paid to environmental issues identified in EIA report and weekly site audit. Mitigation measures recommended in EIA report and Implementation Schedule of Mitigation Measure will be fully implemented.

Construction noise is one of the key environmental issues especially in restricted hours. The conditions stipulated in CNPs should be strictly followed when the construction works were carried out during the restricted hours.

Construction dust is another key environmental issue. The implemented construction dust mitigation measures including covering of exposed slope / soil with tarpaulin sheet etc., should be maintained and improved as necessary. Adequate water spraying should be provided for the unpaved area to minimize dust disturbance.

Water quality impact is also key environmental issue. The drainage system should be well maintained. All wastewater generated within the site should be collected and treated prior to discharge. The solid and liquid waste management should be strictly followed in accordance with the requirements described in the EIA report.

10 Reference

- [1] AECOM Asia Co. Ltd. December 2008. Agreement No. CE 22/2005 (HY) Supplementary No. 1 Traffic Improvements to Tuen Mun Road Town Centre Section – Environmental Monitoring & Audit Manual.

- [2] Ove Arup & Partners Hong Kong Limited. July 2010. Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section – Baseline Monitoring Report (Revision_4).

Appendix A

**Construction
Programme**

HY/2009/03

07-Feb-11?

Design and Build of Traffic Improvement to Tuen Mun Road Town Centre Section

Activity ID	Activity Name	Original Duration	Remainder Duration	Early Start	Early Finish	Late Start	Late Finish	January	February	March	April
								10	11	12	13
								14	15	16	17
								18	19	20	21
								22	23	24	25
								26	27	28	29
								30	31	01	02
								03	04	05	06
								07	08	09	10
								11	12	13	14
								15	16	17	18
								19	20	21	22
								23	24	25	26
								27	28	29	30
								31	01	02	03
								04	05	06	07
								08	09	10	11
								12	13	14	15
								16	17	18	19
								20	21	22	23
								24	25	26	27
								28	29	30	31
								01	02	03	04
								05	06	07	08
								09	10	11	12
								13	14	15	16
								17	18	19	20
								21	22	23	24
								25	26	27	28
								29	30	31	01
								02	03	04	05
								06	07	08	09
								10	11	12	13
								14	15	16	17
								18	19	20	21
								22	23	24	25
								26	27	28	29
								30	31	01	02
								03	04	05	06
								07	08	09	10
								11	12	13	14
								15	16	17	18
								19	20	21	22
								23	24	25	26
								27	28	29	30
								31	01	02	03
								04	05	06	07
								08	09	10	11
								12	13	14	15
								16	17	18	19
								20	21	22	23
								24	25	26	27
								28	29	30	31
								01	02	03	04
								05	06	07	08
								09	10	11	12
								13	14	15	16
								17	18	19	20
								21	22	23	24
								25	26	27	28
								29	30	31	01
								02	03	04	05
								06	07	08	09
								10	11	12	13
								14	15	16	17
								18	19	20	21
								22	23	24	25
								26	27	28	29
								30	31	01	02
								03	04	05	06
								07	08	09	10
								11	12	13	14
								15	16	17	18
								19	20	21	22
								23	24	25	26
								27	28	29	30
								31	01	02	03
								04	05	06	07
								08	09	10	11
								12	13	14	15
								16	17	18	19
								20	21	22	23
								24	25	26	27
								28	29	30	31
								01	02	03	04
								05	06	07	08
								09	10	11	12
								13	14	15	16
								17	18	19	20
								21	22	23	24
								25	26	27	28
								29	30	31	01
								02	03	04	05
								06	07	08	09
								10	11	12	13
								14	15	16	17
								18	19	20	21
								22	23	24	25
								26	27	28	29
								30	31	01	02
								03	04	05	06
								07	08	09	10
								11	12	13	14
								15	16	17	18
								19	20	21	22
								23	24	25	26
								27	28	29	30
								31	01	02	03
								04	05	06	07
								08	09	10	11
								12	13	14	15
								16	17	18	19
								20	21	22	23
								24	25	26	27
								28	29	30	31
								01	02	03	04
								05	06	07	08
								09	10	11	12
								13	14	15	16
								17	18	19	20
								21	22	23	24
								25	26	27	28
								29	30	31	01
								02	03	04	05
								06	07	08	09
								10	11	12	13
								14	15	16	17
								18	19	20	21
								22	23	24	25
								26	27	28	29
								30	31	01	02
								03	04	05	06
								07	08	09	10
								11	12	13	14
								15	16	17	18
								19	20	21	22
								23	24	25	26
								27	28	29	30
								31	01	02	03
								04	05	06	07
								08	09	10	11
								12	13	14	15
								16	17	18	19
								20	21	22	23
								24	25	26	27
								28	29	30	31
								01	02	03	04
								05	06	07	08
								09	10	11	12
								13	14	15	16
								17	18	19	20
								21	22	23	24
								25	26	27	28
								29	30	31	01
								02	03	04	05
								06	07	08	09
								10	11	12	13
								14	15	16	17
								18	19	20	21
								22	23	24	25
								26	27	28	29
								30	31	01	02
								03	04	05	06
								07	08	09	10
								11	12	13	14
								15	16	17	18
								19	20	21	22
								23	24	25	26
								27	28	29	30
								31	01	02	03
								04	05	06	07
								08	09	10	11
								12	13	14	15
								16	17	18	19
								20	21	22	23
								24	25	26	27
								28	29	30	31
								01	02	03	04
								05	06	07	08
								09	10	11	12
								13	14	15	16
								17	18	19	20
								21	22	23	24
								25	26	27	28
								29	30	31	01
</											

HY/2009/03

Design and Build of Traffic Improvement to Tuen Mun Road Town Centre Section

Activity ID	Activity Name	Original Duration	Remaining Duration	Early Start	Early Finish	Late Start	Late Finish	07-Feb-11																
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25
DDAS11120	DDA prepare for Vehicular Bridge S1 Pier & Deck (S abutment to Pier 7)	131	25	31-Jan-11	24-Feb-11	29-Jun-11	23-Jul-11																	
DDAS11130	Submit & endorsed by Statutory Authorities/Government Departments	28	28	25-Feb-11	24-Mar-11	14-Aug-11	11-Sep-11																	
DDAS11135	Final DDA prepare & sub. Vehicular Bridge S1 Pier & Deck (S abutment to Pier 7)	14	14	25-Mar-11	07-Apr-11	11-Sep-11	25-Sep-11																	
DDAS11140	DC DDA certify for Vehicular Bridge S1 Pier & Deck (S abutment to Pier 7)	42	42	25-Feb-11	14-Aug-11	11-Sep-11	25-Sep-11																	
DDAS11150	Submit & Endorsement DDA by SO	35	35	05-Apr-11	12-May-11	25-Sep-11	30-Oct-11																	
DDAS11160	DDA prepare for Vehicular Bridge S1 Pier & Deck (Pier 3 to Pier 7)	114	41	31-Jan-11	13-Jun-11	23-Jul-11	23-Jul-11																	
DDAS11170	Submit & endorsed by Statutory Authorities/Government Departments	28	28	13-Mar-11	09-Apr-11	14-Aug-11	11-Sep-11																	
DDAS11175	Final DDA prepare & sub. Vehicular Bridge S1 Pier & Deck (Pier 3 to Pier 7)	14	14	10-Apr-11	23-Apr-11	11-Sep-11	25-Sep-11																	
DDAS11180	DC DDA certify for Vehicular Bridge S1 Pier & Deck (Pier 3 to Pier 7)	42	42	13-Mar-11	23-Apr-11	14-Aug-11	30-Oct-11																	
DDAS11190	Submit & Endorsement DDA by SO	35	35	24-Apr-11	28-May-11	25-Sep-11	30-Oct-11																	
DDAS11200	DDA prepare for Vehicular Bridge S1 Pier & Deck (N. abutment to Pier 3)	77	70	31-Jan-11	10-Apr-11	15-May-11	23-Jul-11																	
DDAS11210	Submit & endorsed by Statutory Authorities/Government Departments	28	28	11-Apr-11	08-May-11	27-Oct-11	24-Nov-11																	
DDAS11220	DC DDA certify for Vehicular Bridge S1 Pier & Deck (N. abutment to Pier 3)	42	42	11-Apr-11	22-May-11	27-Oct-11	08-Dec-11																	
DDAS11240	DDA prepare for Vehicular Bridge S1 Noise Barrier NE19	60	60	02-Mar-11	30-Apr-11	07-Apr-11	06-Jun-11																	
DDAS11260	DDA prepare for Modification Existing Wong Chi Road	60	60	11-Apr-11	09-Jun-11	24-Jul-11	21-Sep-11																	
Package of Footbridge and Associated Lift																								
Detailed Design Approval (DDA)																								
DDACL1030	Submit & Endorsement DDA by SO	35	1	31-Jan-11	31-Jan-11	22-Mar-11	23-Mar-11																	
DDACL1040	DDA prepare for Chi Lok Bridge Superstructure	90	6	31-Jan-11	31-Jan-11	19-May-11	19-May-11																	
DDACL1050	Submit & endorsed by Statutory Authorities/Government Departments	28	28	31-Jan-11	27-Feb-11	19-May-11	16-Jun-11																	
DDACL1055	Final DDA prepare & sub. Chi Lok Bridge Superstructure	21	21	28-Feb-11	20-Mar-11	16-Jun-11	07-Jul-11																	
DDACL1060	DC DDA certify for Chi Lok Bridge Superstructure	49	49	31-Jan-11	20-Mar-11	19-May-11	07-Jul-11																	
DDACL1070	Submit & Endorsement DDA by SO	35	35	31-Jan-11	24-Apr-11	07-Jul-11	11-Aug-11																	
DDACL1080	DDA prepare for Chi Lok Bridge Architectural Works	60	60	31-Jan-11	31-Mar-11	08-Jun-11	07-Aug-11																	
DDACL1085	Submit & endorsed by Statutory Authorities/Government Departments	28	28	01-Apr-11	28-Apr-11	07-Aug-11	04-Sep-11																	
DDACL1090	Final DDA prepare & sub. Chi Lok Bridge Architectural Works	14	14	29-Apr-11	12-May-11	04-Sep-11	18-Sep-11																	
DDACL1100	DC DDA certify for Chi Lok Bridge Architectural Works	42	42	01-Apr-11	12-May-11	07-Aug-11	18-Sep-11																	
DDASO1000	DDA prepare for Su On Bridge Foundation	60	60	1-Jan-11	31-Jan-11	08-Apr-11	09-Apr-11																	
DDASO1010	Submit & endorsed by Statutory Authorities/Government Departments	28	28	01-Feb-11	26-Feb-11	12-Jul-11	09-Aug-11																	
DDASO1015	Final DDA prepare & sub. Su On Bridge Foundation	14	14	01-Mar-11	14-Mar-11	09-Aug-11	23-Aug-11																	
DDASO1020	DC DDA certify for Su On Bridge Foundation	42	42	01-Feb-11	14-Mar-11	12-Jul-11	23-Aug-11																	
DDASO1030	Submit & Endorsement DDA by SO	35	35	15-Mar-11	18-Apr-11	23-Aug-11	27-Sep-11																	
DDASO1040	DDA prepare for Su On Bridge Superstructure	60	60	01-Feb-11	01-Apr-11	09-Apr-11	08-Jun-11																	
DDASO1050	Submit & endorsed by Statutory Authorities/Government Departments	28	28	02-Apr-11	28-Apr-11	12-Jun-11	10-Jul-11																	
DDASO1055	Final DDA prepare & sub. Su On Bridge Superstructure	14	14	30-Apr-11	13-May-11	10-Jul-11	24-Jul-11																	
DDASO1060	DC DDA certify for Su On Bridge Superstructure	42	42	02-Apr-11	13-May-11	12-Jun-11	24-Jul-11																	
DDASO1080	DDA prepare for Su On Bridge Architectural Works	60	60	02-Apr-11	31-May-11	08-Jun-11	07-Aug-11																	
DDAYC1030	Submit & Endorsement DDA by SO	35	2	31-Jan-11	01-Feb-11	08-Feb-11	07-Aug-11																	
DDAYC1055	Final DDA prepare & sub. Yan Ching Bridge Superstructure	14	14	31-Jan-11	31-Jan-11	13-Feb-11	14-Feb-11																	
DDAYC1060	DC DDA certify for Yan Ching Bridge Superstructure	42	42	31-Jan-11	31-Jan-11	13-Feb-11	14-Feb-11																	
DDAYC1070	Submit & Endorsement DDA by SO	35	35	01-Feb-11	07-Mar-11	14-Feb-11	21-Mar-11																	
DDAYC1080	DDA prepare for Yan Ching Bridge Architectural Works	28	20	31-Jan-11	05-Feb-11	09-Feb-11	01-Mar-11																	
DDAYC1095	Final DDA prepare & sub. Yan Ching Bridge Architectural Works	14	14	20-Feb-11	05-Mar-11	14-Mar-11	15-Mar-11																	
DDAYC1096	DC DDA certify for Yan Ching Bridge Architectural Works	42	42	05-Mar-11	09-Apr-11	15-Mar-11	19-Apr-11																	
DDAYC1100	Submit & Endorsement DDA by SO	6	1	31-Jan-11	31-Jan-11	19-Apr-11	20-Apr-11																	
DDAYC1110	Final DDA prepare & sub. Yan Ching Bridge Foundation	42	42	31-Jan-11	31-Jan-11	19-Apr-11	20-Apr-11																	
DDAYC1015	DC DDA certify for Yan Ching Bridge Foundation	35	35	01-Feb-11	27-Feb-11	28-Feb-11	25-May-11																	
DDAYC1020	Submit & Endorsement DDA by SO	60	60	31-Jan-11	31-Jan-11	25-May-11	25-May-11																	
DDAYC1030	DDA prepare for Yan Ching Bridge Superstructure	28	28	01-Feb-11	28-Feb-11	28-Feb-11	26-Mar-11																	
DDAYC1040	Submit & endorsed by Statutory Authorities/Government Departments	14	14	01-Mar-11	28-Mar-11	28-Mar-11	11-Apr-11																	
DDAYC1050	Final DDA prepare & sub. Yan Ching Bridge Superstructure	42	42	01-Feb-11	28-Feb-11	28-Mar-11	11-Apr-11																	
DDAYC1055	DC DDA certify for Yan Ching Bridge Superstructure	35	35	01-Feb-11	28-Feb-11	28-Mar-11	11-Apr-11																	
DDAYC1060	Submit & Endorsement DDA by SO	60	60	01-Feb-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1070	Final DDA prepare & sub. Yan Ching Bridge Architectural Works	14	14	02-Apr-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1080	DC DDA certify for Yan Ching Bridge Architectural Works	35	35	02-Apr-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1090	DDA prepare for Yan Ching Bridge Foundation	28	28	02-Apr-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1095	Submit & Endorsement DDA by SO	60	60	02-Apr-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1100	Final DDA prepare & sub. Yan Ching Bridge Foundation	14	14	02-Apr-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1015	DC DDA certify for Yan Ching Bridge Foundation	35	35	02-Apr-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1020	Submit & Endorsement DDA by SO	60	60	02-Apr-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1030	Final DDA prepare & sub. Yan Ching Bridge Foundation	14	14	02-Apr-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1040	DC DDA certify for Yan Ching Bridge Foundation	35	35	02-Apr-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1050	Submit & Endorsement DDA by SO	60	60	02-Apr-11	28-Apr-11	18-Aug-11	15-Sep-11																	
DDAYC1055	Final DDA prepare & sub. Yan Ching Bridge Foundation	14	14																					

HY/2009/03

07-Feb-11?

Design and Build of Traffic Improvement to Tuen Mun Road Town Centre Section

Activity ID	Activity Name	Original Duration	Remaining Duration	Early Start	Early Finish	Late Start	Late Finish	January	February	March	April
								03 10 17 24	31 07 14 21 28 04 11 18 25	13 20 27 04 11 18 25	10 17 24 31 07 14 21 28 04 11 18 25
DDAVO1095	Final DDA prepare & sub. Yan Oi Bridge Architectural Works	14	14	30-Apr-11	13-May-11	15-Sep-11	20-Sep-11				
DDAVO1100	DC DDA certify for Yan Oi Bridge Architectural Works	42	42	02-Apr-11	13-May-11	18-Aug-11	29-Sep-11				
DDAZL1010	Submit & endorsed by Statutory Authorities/Government Departments	28	1	31-Jan-11	30-Mar-11	31-Mar-11	31-Mar-11				
DDAZL1020	Final DDA prepare & sub. Footbridge Lift	14	14	01-Feb-11	14-Feb-11	31-Mar-11	14-Apr-11				
DDAZL1030	DC DDA certify for Footbridge Lift	42	15	31-Jan-11	30-Mar-11	30-Mar-11	14-Apr-11				
DDAZL1040	Submit & Endorsement DDA by SO	35	35	15-Feb-11	21-Mar-11	14-Apr-11	19-May-11				
Package of LRT Passenger Lift											
Detailed Design Approval (DDA)											
DDAPL1055	Final DDA prepare & sub. Passenger Lift E&M, Lift & Architectural Works	23	9	31-Jan-11	09-Feb-11	24-Feb-11	05-Mar-11				
DDAPL1060	DC DDA certify for Passenger Lift E&M, Lift & Architectural Works	42	9	31-Jan-11	09-Feb-11	24-Feb-11	04-Mar-11				
DDAPL1070	Submit & Endorsement DDA by SO	35	35	09-Feb-11	15-Mar-11	04-Mar-11	09-Apr-11				
Package of Geotechnical Works											
Detailed Design Approval (DDA)											
DDAGE1030	Submit & endorsed by GEO	28	4	31-Jan-11	03-Feb-11	09-Mar-11	13-Mar-11				
DDAGE1040	DDA prepare for Reinforced Earth Wall GSW-AFR10	30	4	31-Jan-11	03-Feb-11	28-Mar-11	01-Apr-11				
DDAGE1110	Submit & endorsed by Statutory Authorities/Government Departments	28	28	04-Feb-11	03-Mar-11	01-Apr-11	29-Apr-11				
DDAGE1115	Final DDA prepare & sub. Reinforced Earth Wall GSW-AFR10	14	14	04-Mar-11	17-Mar-11	29-Apr-11	13-May-11				
DDAGE1120	DC DDA certify for Reinforced Earth Wall GSW-AFR10	42	42	04-Feb-11	17-Mar-11	13-May-11	24-Jun-11				
DDAGE1130	Submit & endorsed by GEO	28	28	18-Mar-11	14-Apr-11	24-Jun-11	22-Jul-11				
DDAGE1140	Submit & Endorsement DDA by SO	35	35	15-Apr-11	19-May-11	22-Jul-11	26-Aug-11				
DDAGE1150	DDA prepare for Slope Works	60	60	18-Mar-11	16-May-11	13-May-11	12-Jul-11				
Package of Drainage Works											
Detailed Design Approval (DDA)											
DDADG1070	Submit & Endorsement DDA by SO	35	1	31-Jan-11	31-Jan-11	24-Aug-11	25-Aug-11				
DDADG1110	Submit & Endorsement DDA by SO	35	4	31-Jan-11	03-Feb-11	12-Feb-11	21-Feb-11				
Package of Provisional Works for TCSS Installation											
Detailed Design Approval (DDA)											
DDATS1030	Submit & Endorsement DDA by SO	35	1	31-Jan-11	31-Jan-11	27-Mar-11	28-Mar-11				
Package of At-Grade Irrigation System											
Detailed Design Approval (DDA)											
DDAIS1000	DDA prepare for At-grade Irrigation Systems	120	69	31-Jan-11	09-Apr-11	31-Jan-11	10-Apr-11				
DDAIS1010	Submit & endorsed by Statutory Authorities/Government Departments	28	28	10-Apr-11	07-May-11	09-Jun-11	07-Jul-11				
DDAIS1020	DC DDA certify for At-grade Irrigation Systems	42	42	10-Apr-11	22-May-11	09-Jun-11	21-Jul-11				
Package of Landscaping Works											
Detailed Design Approval (DDA)											
DDALW1000	DDA prepare for At-grade Landscaping Works	60	60	10-Apr-11	09-Jun-11	10-Apr-11	09-Jun-11				
DDALW1040	DDA prepare for Noise Barrier/Enclosure Landscaping Works	120	22	31-Jan-11	21-Feb-11	13-Mar-11	03-Apr-11				
DDALW1050	Submit & endorsed by Statutory Authorities/Government Departments	28	28	22-Feb-11	21-Mar-11	04-Apr-11	01-May-11				
DDALW1055	Final DDA prepare & sub. Noise Barrier/Enclosure Landscaping Works	14	14	22-Mar-11	04-Apr-11	02-May-11	15-May-11				
DDALW1060	DC DDA certify for Noise Barrier/Enclosure Landscaping Works	42	42	22-Feb-11	04-Apr-11	04-Apr-11	15-May-11				
DDALW1070	Submit & Endorsement DDA by SO	35	35	05-Apr-11	09-May-11	18-May-11	19-Jun-11				
Project General Submission											
General Submission											
Initial Submission											
GS1010	Spores to enable WSD to decide on the quantities and type	0	0	28-Feb-11	28-Feb-11	28-Feb-11	28-Feb-11				
GS1140	Produce the web site	0	0	31-Jan-11	28-Feb-11	28-Feb-11	31-Jan-11				
GS1170	Proposed plans for release of video	0	0	28-Feb-11	28-Feb-11	28-Feb-11	31-Jan-11				
GS1230	Utilities survey	0	0	31-Mar-11	30-Apr-11	30-Apr-11	30-Apr-11				
GS1350	Weather protection scheme	0	0	30-Apr-11	30-Apr-11	30-Apr-11	30-Apr-11				
GS1510	Submit temporary bridge (Yan Oi)	204	34	31-Jan-11	05-Mar-11	19-Feb-11	25-Mar-11				
GS1515	Submit temporary bridge (Ching Lok)	217	35	31-Jan-11	06-Mar-11	01-Feb-11	08-Mar-11				
GS1540	Sub. & app. tree survey report	14	1	31-Jan-11	31-Jan-11	25-Aug-11	25-Aug-11				

Remaining Level of Effort	Actual Work	3 Months Rolling Programme (cutoff: 31-01-11)	Date	Revision	Checked
Actual Level of Effort	Remaining ...		23-Dec-11	1012	Tim
			07-Feb-11	1101	Tim

07-Feb-11?

Activity ID	Activity Name	Original Duration	Remaining Duration	Early Start	Early Finish	Late Start	Late Finish
GS1650	Investigation works for vicinity of petrol station	45	45	01-Apr-11	30-May-11	04-Jul-14	28-Aug-14
Trail Piles for Friction Piles							
GS1660	Trail piles & test for friction piles	55	11	31-Jan-11	15-Feb-11	02-Feb-11	18-Feb-11
Trail Green Panel							
GS1670	Prepare green wall panel for on site trail	75	49	31-Jan-11	31-Mar-11	15-Feb-12	14-Apr-12
GS1680	Site trail for green wall panel	365	365	01-Apr-11	30-Mar-12	16-Apr-12	15-Apr-13
GS1690	Prepare green roof trail	75	71	31-Jan-11	30-Apr-11	17-Jan-12	14-Apr-12
Procurement							
Material Procurement and Fabrication							
Procurement and Fabrication							
MP1000	Temporary Bridge near Yuen Oi Bridge	90	12	31-Jan-11	16-Feb-11	19-Feb-11	05-Mar-11
MP1010	Temporary Bridge near Chi Lok Bridge	90	26	31-Jan-11	05-Mar-11	01-Feb-11	07-Mar-11
MP1040	Yuen Ching Bridge span	90	90	31-Mar-11	13-Jul-11	29-Mar-11	15-Jul-11
MP1050	Yuen Ching Bridge Passenger Lift	90	90	15-Mar-11	07-Jul-11	29-Apr-11	17-Aug-11
MP1000	Noise Barrier/Enclosure steel structure for Scheme A Area	570	570	15-Mar-11	15-Feb-13	04-May-11	15-Feb-13
MP1110	Noise Barrier/Enclosure steel structure for Scheme B Area	534	534	25-Apr-11	05-Feb-13	28-Apr-11	09-Feb-13
MP1130	Noise Barrier/Enclosure steel structure for Scheme D Area	613	613	16-Apr-11	11-May-13	28-May-11	13-May-13
MP1250	LRT Passenger Lift structure	90	27	31-Jan-11	05-Mar-11	13-Apr-11	16-May-11
MP1260	LRT Passenger Lift	90	32	31-Jan-11	11-Mar-11	13-May-11	22-Jun-11
Section 1 of Works							
Tuen Hing Road /Castle Peak Road							
Improvement Works at Tuen Hing Road /Castle Peak Road							
Tree Felling and Transplanting							
SEC11100	Tree transplanting	90	23	31-Jan-11	01-Mar-11	21-Jan-11	18-Jul-11
Drainage Works							
SEC1120	Construct drainage near Tuen Mun Woman Health Centre	60	60	02-Mar-11	16-May-11	19-Jul-11	27-Sep-11
Fu Fat Lane / Castle Peak Road							
Improvement Works at Fu Fat Lane / Castle Peak Road							
Temporary Traffic Arrangement							
SEC11270	Submit and approve TTA for re-align existing footpath along Yuen Long bound slow lane	120	1	31-Jan-11	31-Jan-11	01-Feb-11	01-Feb-11
Tree Felling and Transplanting							
SEC11110	Tree felling and transplanting	90	90	01-Feb-11	26-May-11	02-Feb-11	27-May-11
Hoi Wing Road / Castle Peak Road							
Improvement Works at Hoi Wing Road / Castle Peak Road							
Temporary Traffic Arrangement							
SEC11280	Submit and approve TTA for re-align existing footpath along Kowloon bound and new slip road	120	1	31-Jan-11	31-Jan-11	08-Feb-11	08-Feb-11
Tree Felling and Transplanting							
SEC11120	Tree felling and transplanting	60	10	31-Jan-11	14-Feb-11	08-Feb-11	18-Feb-11
Drainage Works							
SEC11460	Construct drainage along Kowloon bound	80	80	15-Feb-11	25-May-11	19-Feb-11	30-May-11
Roadworks							
SEC11210	Relocation existing street lighting and re-align existing footpath along Kowloon bound	70	70	19-Apr-11	13-Jul-11	23-Apr-11	18-Jul-11
Tsing Wui Street							
Construction for New Carpark at Tsing Wui Street							
Temporary Traffic Arrangement							
SEC11030	Submit and approve TTA for Tsing Wui St car parking	120	26	31-Jan-11	24-Feb-11	30-Apr-11	25-May-11
Roadworks							
SEC11000	Construct new car parking spaces	60	60	26-Feb-11	11-Mar-11	26-May-11	05-Jun-11
Submit and approve TTA for Tsing Wui St car parking							

Remaining Level of Effort	Actual Work	3 Months Rolling Programme (cutoff: 31-01-11)			Approved
		Date	Revision	Checked	Approved

3 Months Rolling Programme (cutoff: 31-01-11)		Date	Revision	Checked	Approved
Remaining Level of Effort	██████████	23-Dec-...	1012	Tim	
Actual Level of Effort	██████████	07-Feb-...	1101	Tim	

Page 4 of 9

HY/2009/03

07-Feb-11?

Design and Build of Traffic Improvement to Tuen Mun Road Town Centre Section

Activity ID	Activity Name	Original Duration	Remaining Duration	Early Start	Early Finish	Late Start	Late Finish	January	February	March	April
								03 10 17 24 31	07 14 21 28	04 11 18 25	
Tsing Sin Street											
Construction of New Carpark at Tsing Sin Street											
Temporary Traffic Arrangement											
SEC11040	Submit and approve TTA for Tsing Sin St car parking	120	25	31-Jan-11	24-Feb-11	30-Apr-11	25-May-11				
Roadworks											
SEC11010	Construct new car parking spaces	60	60	25-Feb-11	11-May-11	25-May-11	05-Aug-11				
Tsing Wui Street (near Kai Hei Land Bldg)											
Construction of New Carpark at Tsing Wui Street (near Kai Hei Land Bldg)											
Temporary Traffic Arrangement											
SEC11050	Submit and approve TTA for Tsing Wui St near Haland Bldg car parking	120	25	31-Jan-11	24-Feb-11	25-Mar-11	18-Apr-11				
Tree Felling and Transplanting											
SEC11410	Tree felling and transplanting	60	60	24-Feb-11	11-May-11	25-May-11	05-Aug-11				
Roadworks											
SEC11020	Construct new car parking spaces	90	90	24-Feb-11	17-Jun-11	18-Apr-11	05-Aug-11				
Section II of Works											
Scheme A (CH29405 - CH29050)											
Stage 1											
Tree Felling and Transplanting											
RA1000	Tree felling and transplanting for Yan Oi Tong Circuit	90	1	31-Jan-11	31-Jan-11	21-Feb-11	22-Feb-11				
Temporary Traffic Arrangement											
RA1605	Realign existing central median along NE01	45	2	31-Jan-11	01-Feb-11	31-Jan-11	02-Feb-11				
Utilities Diversion											
RA1660	Temporary diversion existing 12kv & 11kv cable (132KV-1 & 11KV-1) for NE01 & NE02	40	23	31-Jan-11	01-Mar-11	31-Jan-11	02-Mar-11				
RA1670	Drainage diversion for existing 450 dia & 525 dia pipe for NE01	45	24	31-Jan-11	02-Mar-11	29-Jan-11	02-Mar-11				
Site Investigation/Pre-drilling Works											
RA1610	Pre-drilling works for NB foundation NE01 PC1 to PC8	21	21	02-Feb-11	01-Mar-11	02-Feb-11	02-Mar-11				
Foundation Works											
RA1630	Construct Socket H-piles foundation for NE01 PC1 to PC8 (33nos, 610mm)	66	66	02-Mar-11	25-May-11	02-Mar-11	25-May-11				
RA1680	Construct part of pile cap NE01 PC1 to PC8	64	64	14-Apr-11	02-Jul-11	31-May-11	16-Aug-11				
RA1690	Temporary support and remove existing retaining wall for NE03 FT1 to FT4	80	80	31-Jan-11	18-Apr-11	19-Mar-11	04-Jun-11				
RA1100	Construct pile footing NE03 FT1 to FT4	64	64	19-Apr-11	06-Jul-11	04-Jun-11	20-Aug-11				
Stage 2											
Utilities Diversion											
RA1680	Relocation existing draw pit (HKTS-3) for NE05	60	60	28-Feb-11	14-May-11	13-Aug-11	26-Oct-11				
Construction of temporary Yan Oi Bridge											
Temporary Bridge Structural Steel Frame Erection											
TB1020	Erect N/B temporary bridge span	7	7	17-Feb-11	24-Feb-11	05-Mar-11	14-Mar-11				
TB1030	Erect S/B temporary bridge span	7	7	25-Feb-11	04-Mar-11	14-Mar-11	22-Mar-11				
E&M and Finishing Works											
TB1040	Finishing & E&M works	36	36	05-Mar-11	19-Apr-11	22-Mar-11	07-May-11				
Construction of New Yan Oi Bridge											
Temporary Traffic Arrangement											
YO1460	Submit and approve TTA for Yan Oi Bridge central median	120	120	30-Mar-11	27-Jul-11	15-Apr-11	13-Aug-11				
Demolition of Existing Yan Oi Bridges											
TB1005	Demolition existing Yan Oi bridge S/B ramp	31	22	31-Jan-11	01-Feb-11	01-Feb-11	02-Mar-11				
TB1050	Demolition existing Yan Oi bridge span and mid column	30	30	20-Apr-11	26-May-11	07-May-11	13-Jun-11				
Utilities Diversion											
YO1160	Temporary diversion existing 12kv & 11kv cable (132KV-1 & 11KV-2)	60	60	31-Jan-11	18-Apr-11	09-Mar-11	25-May-11				
YO1200	Drainage diversion for existing 450 dia & 525 dia pipe	60	60	31-Jan-11	18-Apr-11	09-Mar-11	25-May-11				
Site Investigation/Pre-drilling Works											
YO1000	Pre-drilling works for New Yan Oi bridge S/B PC1 to PC3	21	21	01-Mar-11	24-Mar-11	29-Apr-11	25-May-11				

Remaining Level of Effort ☐ Actual Work ☐

Actual Level of Effort ☐ Remaining ... ☐

3 Months Rolling Programme (cutoff: 31-01-11)

Date Revision Checked

23-Dec... 1012 Tim

07-Feb... 1101 Tim

Approved

07-Feb-11?

2070

Activity ID	Activity Name	Original Duration	Remaining Duration	Early Start	Early Finish	Late Start	Late Finish	January	February	March	April
								03	10	17	24
Construction of New Yan Ching Bridge											
Temporary Traffic Arrangement											
YC1150	Submit and approve TTA for Yan Ching Bridge central median construction	120		1-Jan-11	31-Jan-11	25-Mar-11	25-Mar-11				
YC1160	Submit and approve TTA for Yan Ching Bridge NIB construction	120		1-Jan-11	31-Jan-11	07-Feb-11	08-Feb-11				
Utilities Diversion											
YC1220	Temporary slew existing PCW cable (HK2-2)	0		0-Jan-11	24-Mar-11	26-Mar-11	26-Mar-11				
YC1230	Diversion existing watermain (WS-2)	0		0-Jan-11	24-Mar-11	26-Mar-11	26-Mar-11				
Piling Works											
YC1000	Foundation for New Yan Ching bridge PC1 & PC3 (15nos, pre-bore H-pile)	45		15-Feb-11	13-Apr-11	22-Feb-11	21-Apr-11				
YC1120	Foundation for New Yan Ching bridge PC2 & PC5 (15nos, pre-bore H-pile)	45		02-Feb-11	23-Mar-11	09-Feb-11	26-Mar-11				
YC1130	Foundation for New Yan Ching bridge PC4 (6nos, pre-bore H-pile)	18		18-Mar-11	19-Apr-11	26-Mar-11	21-Apr-11				
YC1140	Pile Test	21		19-Apr-11	14-May-11	05-May-11	31-May-11				
Pile Cap											
YC1010	Construct pile cap PC1 & PC3	48		13-Apr-11	10-Jun-11	21-Apr-11	20-Jun-11				
YC1170	Construct pile cap PC2 & PC5	48		24-Mar-11	21-Apr-11	21-Apr-11	20-Jun-11				
YC1180	Construct pile cap PC4	32		19-Apr-11	25-May-11	21-Apr-11	31-May-11				
Scheme B (CH29050 - CH28520)											
Stage 1											
Temporary Traffic Arrangement											
RB1820	Submit and approve TTA for RB Stage 1 SB extend to Tuen Lee Street	120		28-Jan-11	28-Feb-11	09-Mar-11	07-Apr-11				
RB1830	Submit and approve TTA for RB Stage 1 NB extend to Tuen Lee Street	120		28-Jan-11	28-Feb-11	09-Mar-11	07-Apr-11				
Tree Felling and Transplanting											
RB1150	Tree Felling and Transplanting up to TMTP	60		1-Jan-11	31-Jan-11	05-May-11	06-May-11				
RB1160	Tree Felling and Transplanting extend to Tuen Lee Street	90		1-Jan-11	31-Jan-11	09-May-11	10-May-11				
RB2010	Tree felling and transplanting along Tuen Fat & Tuen Hi road	120		4-Jan-11	07-Feb-11	26-Apr-12	04-May-12				
Utilities Diversion											
RB1760	Drainage diversion for existing 600 dia pipe for NE09	0		0-Jan-11	31-Jan-11	02-Feb-11	02-Feb-11				
RB1840	Drainage diversion for existing 450 dia pipe for NE06	60		22-Jan-11	28-Feb-11	17-Mar-11	16-Apr-11				
RB1860	Reclamation existing drawing pit (HK2-6) for NE06	30		04-Mar-11	13-Apr-11	09-May-11	16-Apr-11				
Site Investigation/Precasting Works											
RB1840	Pre-drilling works for NE12 PC5	30		31-Jan-11	21-Feb-11	11-Aug-11	30-Aug-11				
Foundation Works											
RB1180	Construct Socket H-piles foundation for NE08 PC1 to PC5 (32nos, 610mm)	97		15-Feb-11	15-Jun-11	06-May-11	30-Aug-11				
RB1190	Construct Mini piles foundation for NE09 PC1 to PC10 (74nos, mini pile)	112		31-Jan-11	10-May-11	02-Feb-11	13-May-11				
RB1200	Construct Mini piles foundation for NE09 PC11 to PC20 (74nos, mini pile)	112		31-Jan-11	14-Jun-11	03-Mar-11	14-Jul-11				
Pile Cap Footing											
RB1270	Construct pad footing for NE10 FT1 to FT8 & NE11 FT1 to FT8	133		02-Mar-11	13-Aug-11	10-Mar-11	23-Aug-11				
RB1280	Construct pile cap for NE09 PC11 to PC20	167		14-Apr-11	02-Nov-11	13-May-11	30-Nov-11				
RB1300	Construct pad footing for NE10 FT7 to FT24 & NE11 FT15 to FT22	133		02-Mar-11	13-Aug-11	10-Mar-11	23-Aug-11				
RB1320	Construct pad footing for NE06 FT13 to FT18	100		13-Apr-11	12-Aug-11	16-Apr-11	16-Aug-11				
Relocation of LRT Passenger Lift											
Utilities Diversion											
LRT1020	Drainage diversion existing 450 dia x2 pipe	80		13-Jan-11	31-Jan-11	07-Feb-11	08-Feb-11				
Piling Works											
LRT1090	Construct Socket H-pile foundation (4nos, 610mm)	12		01-Feb-11	18-Feb-11	08-Feb-11	22-Feb-11				

07-Feb-11?

www.tfpassociati.it

Activity ID	Activity Name	Original Duration	Remaining Duration	Early Start	Early Finish	Late Start	Late Finish
RC1600	Rehabration existing fire hydrant (WS-8) for NE16 FT27 to FT34 & PC35	60	18	31-Jan-11	23-Feb-11	09-Jun-11	02-Jul-11
RC1610	Temporary slow existing 11kv & 132kv cable (132KV-4 & 11KV-9) for NE16 FT27 to FT34 & PC35	90	39	31-Jan-11	19-Mar-11	14-May-11	02-Jul-11
RC1620	Diversion existing 300 dia drainage pipe for NE16 FT27 to FT34	45	45	31-Jan-11	26-Mar-11	07-May-11	02-Jul-11
Site Investigation/Pre-drilling Works							
RC1625	Pre-drilling works for NB foundation NE16 PC1 to PC8 & NE16 PC10	30	30	01-Mar-11	08-Apr-11	30-Mar-11	10-May-11
RC1630	Pre-drilling works for NB foundation NE16 PC35	14	14	09-Apr-11	25-Apr-11	02-Jul-11	18-Jul-11
RC1635	Construct Socket H-piles foundation for NE15 PC1 to PC9 & NE16 PC10 (28nos, 610mm)	85	85	22-Apr-11	03-Aug-11	10-May-11	20-Aug-11
Foundation Works							
RC1200	Construct drainage along Bang Ha Circuit	62	62	07-Feb-11	23-Apr-11	21-Feb-11	10-May-11
RC1020	Road re-alignment along Tang Hoi Circuit	70	70	14-Mar-11	09-Jun-11	29-Mar-11	25-Jun-11
Construction of Temporary Chi Lok Bridge							
Utilities Diversion							
TB2080	Temporary slow existing Telecom cable for SB footing	60	60	31-Jan-11	18-Apr-11	04-Mar-11	18-May-11
TB2100	Temporary slow existing Telecom 11kv & 132kv cable for SB footing	60	60	31-Jan-11	18-Apr-11	04-Mar-11	18-May-11
TB2110	Diversion existing gasmain for SB	60	11	31-Jan-11	15-Feb-11	04-Mar-11	17-Mar-11
TB2120	Temporary slow existing Telecom 11kv & 132kv cable for NB footing	60	60	31-Jan-11	18-Apr-11	23-Feb-11	10-May-11
Quail Stone Installation							
TB2160	Erect NB steel column	10	10	31-Jan-11	14-Feb-11	23-Feb-11	07-Mar-11
TB2160	Erect CM steel column	21	21	31-Jan-11	26-Feb-11	10-Feb-11	07-Mar-11
TB2170	Erect SB access ramp	45	45	31-Jan-11	26-Mar-11	04-Mar-11	30-Apr-11
TB2180	Erect NB access ramp	45	45	31-Jan-11	26-Mar-11	04-Mar-11	30-Apr-11
Temporary Bridge Structural Steel Panel Erection							
TB2020	Erect NB temporary bridge span	14	14	03-Mar-11	22-Mar-11	07-Mar-11	23-Mar-11
TB2030	Erect SB temporary bridge span	14	14	22-Mar-11	12-Apr-11	23-Mar-11	13-Apr-11
EAM and Finishing Works							
TB2040	Finishing & EAM works	45	45	12-Apr-11	06-Jun-11	13-Apr-11	07-Jun-11
Construction of Retaining Wall GSW-AFR33							
Temporary Traffic Arrangement							
RW1040	Submit and approve ITA for construction GSW-AFR33	120	120	31-Jan-11	31-Jan-11	04-Mar-11	05-Mar-11
Tree Felling and Transplanting							
RW1050	Tree felling and transplanting	90	90	31-Jan-11	07-Feb-11	04-Mar-11	09-Mar-11
RW1050A-FR33	Construct retaining wall GSW-AFR33 (Base Slab) (3 bays)	50	50	08-Feb-11	11-Apr-11	09-Mar-11	12-May-11
RW1010	Construct retaining wall GSW-AFR33 (Wall)	50	50	01-Mar-11	03-May-11	30-Mar-11	03-Jun-11
Section III of Works							
Scheme D (CH28200 - CH27785)							
Stage 1							
Tree Felling and Transplanting							
RD1780	Tree transplanting for NE26 PC1 to PC10	60	1	31-Jan-11	31-Jan-11	02-Apr-11	08-Apr-11
Utilities Diversion							
RD1190	Diversion existing 1050 dia drainage pipe for NE20 PC10 to PC14 & NE25 PC1 to PC7	90	22	31-Jan-11	28-Feb-11	01-Feb-11	02-Mar-11
RD1240	Pre-drilling works for NB foundation NE20 PC10 to PC14 & NE25 PC1 to PC7	22	22	31-Jan-11	28-Feb-11	01-Feb-11	02-Mar-11
Foundation Works							
RD1250	Construct Socket H-piles foundation for NE20 PC10 to PC14 (28nos, 610mm)	85	85	01-Mar-11	14-Jun-11	02-Mar-11	15-Jun-11
RD1260	Construct Mini-piles foundation for NE25 PC1 to PC7 (31nos, mini pile)	94	94	01-Mar-11	25-Jun-11	03-Mar-11	29-Jun-11
RD1670	Construct Socket H-piles foundation for NE26 PC1 to PC10 (46nos, 610mm)	70	70	01-Feb-11	30-Apr-11	08-Apr-11	04-Jul-11
Pile cap / Footing							
RD1270	Construct pile cap NE20 PC10 to PC14	83	83	25-Apr-11	04-Aug-11	26-Apr-11	05-Aug-11
RD1530	Construct pile cap NE25 PC1 to PC7	117	117	29-Apr-11	18-Sep-11	03-May-11	19-Sep-11
RD1710	Construct pile cap and wall NE26 PC1 to PC10	83	83	10-Feb-11	25-May-11	14-Apr-11	25-Jul-11
Construction of Vehicular Bridge S1							

3 Months Rolling Programme (cutoff: 31-01-11)	Date	Revision	Checked	Approved
Remaining Level of Effort	Actual Work			

Actual Level of Effort	Remaining ...
23-Dec...	23-Dec...
1012	1012
Tim	Tim

HY/2009/03

Design and Build of Traffic Improvement to Tuen Mun Road Town Centre Section

07-Feb-11?

Activity ID	Activity Name	Original Duration	Remaining Duration	Early Start	Early Finish	Late Start	Late Finish	Jan-11	Feb-11	Mar-11	Apr-11	May-11	Jun-11	Jul-11	Aug-11	Sep-11	Oct-11	Nov-11	Dec-11
Temporary Traffic Arrangement																			
S1B1020	Submit and approve TTA for Pier 3 to Pier 7	120	120	01-Apr-11	30-Jul-11	07-Apr-11	05-Aug-11												
Utilities Division																			
S1B1030	Temporary slew existing 132kv cable (132KV-10) for Pier 10	90	90	19-Apr-11	05-Aug-11	19-Apr-11	05-Aug-11												
Scheme E (CH27785 - CH27000)																			
Stage 4																			
Roadworks																			
RE11160	Existing S16 road reconstruction SL CH27550 to CH27750	67	67	01-Feb-11	27-Apr-11	29-Mar-11	23-Jun-11												
RE11170	Existing S16 road reconstruction ML CH27550 to CH27750	67	67	27-Apr-11	19-Jul-11	23-Jun-11	09-Sep-11												
Construction of Reinforced Earth Wall GSW-AFR10																			
Compensatory Traffic Arrangement																			
REW1020	Submit and approve TTA RE wall at Castle Peak Road	120	78	31-Jan-11	18-Apr-11	31-Jan-11	18-Apr-11												
REW1030	Tree felling and transplanting	90	90	18-Apr-11	05-Aug-11	07-Sep-11	24-Dec-11												
Section IIIC of Works																			
General Submission																			
Landscaping Works																			
P4GN1030	Order & delivery tree pot	35	1	31-Jan-11	31-Jan-11	19-Nov-10	19-Nov-10												
P4GN1040	Excavation permit for Section 3C, 3E and 3G area	65	1	31-Jan-11	31-Jan-11	19-Nov-10	19-Nov-10												
Landscaping Works in Portion 4																			
Landscaping Works																			
3C1010	Compensatory planting works at Location No 27 (6 nos.)	18	18	07-Mar-11	30-Mar-11	11-Jan-11	03-Feb-11												
3C1020	Compensatory planting works at Location No 28 (8 nos.)	18	18	23-Mar-11	15-Apr-11	27-Jan-11	21-Feb-11												
3C1030	Compensatory planting works at Location No 29 (8 nos.)	18	18	01-Feb-11	08-Dec-10	31-Dec-10	31-Dec-10												
3C1050	Compensatory planting works at Location No 30A (7 nos. tree pot)	18	18	09-Feb-11	04-Mar-11	10-Feb-11	07-Mar-11												
3C1070	Compensatory planting works at Location No 31A (1 nos.)	18	18	08-Apr-11	03-May-11	14-Feb-11	09-Mar-11												
3C1080	Compensatory planting works at Location No 31B	60	60	31-Jan-11	22-Apr-11	06-Dec-10	25-Feb-11												
3C1090	Compensatory planting works at Location No 32 (4 nos.)	18	18	17-Feb-11	14-Mar-11	24-Dec-10	19-Jan-11												
3C1100	Compensatory planting works at Location No 33 (3 nos. tree pot)	12	12	01-Feb-11	16-Feb-11	02-Feb-11	17-Feb-11												
3C1150	Compensatory planting works at Location No 34C (5 nos.)	18	18	23-Mar-11	15-Apr-11	27-Jan-11	21-Feb-11												
Establishment Works																			
3C1170	Establishment Works (Nos. 26, 27, 28, 29, 30, 30A, 31, 31A, 31B, 32, 33, 33B, 34, 34A, 34B, 34C and 35)	365	365	26-Feb-11	25-Feb-12	26-Feb-11	25-Feb-12												
Section IIIE of Works																			
Landscaping Works in Portion 4																			
Landscaping Works																			
3E1080	Establishment Works (Nos. 46, 46A, 46B, 47A, 47C, 47D, 47E & 47F)	365	365	26-Feb-11	25-Feb-12	26-Feb-11	25-Feb-12												
Section IIIG of Works																			
Landscaping Works in Portion 4																			
Landscaping Works																			
3G1010	Compensatory planting works at Location No 2 (3 nos.)	12	12	25-Feb-11	14-Mar-11	16-Dec-10	31-Dec-10												
3G1030	Compensatory planting works at Location No 5 (3 nos. tree pot)	12	12	07-Mar-11	22-Mar-11	24-Dec-10	10-Jan-11												
3G1040	Compensatory planting works at Location No 6 (2 nos. tree pot)	12	12	15-Mar-11	30-Mar-11	03-Jan-11	18-Jan-11												
3G1050	Compensatory planting works at Location No 8 (2 nos. tree pot)	12	12	29-Mar-11	07-Apr-11	11-Jan-11	26-Jan-11												
3G1060	Compensatory planting works at Location No 9 (2 nos. tree pot)	12	12	31-Mar-11	15-Apr-11	19-Jan-11	03-Feb-11												
3G1070	Compensatory planting works at Location No 10 (9 nos.)	18	18	18-Apr-11	11-May-11	04-Feb-11	01-Mar-11												
3G1090	Compensatory planting works at Location No 13 (10 nos.)	18	18	01-Feb-11	24-Feb-11	22-Nov-10	15-Dec-10												

Remaining Level of Effort	Actual Work	3 Months Rolling Programme (cutoff: 31-01-11)	Date	Revision	Checked	Approved
Actual Level of Effort	Remaining ...		23-Dec-11	1012	Tim	
			07-Feb-11	1101	Tim	

HY/2009/03

07-Feb-11?

Design and Build of Traffic Improvement to Tuen Mun Road Town Centre Section

Activity ID	Activity Name	Original Duration	Remaining Duration	Early Start	Early Finish	Late Start	Late Finish	January	February	March	April
3G1100	Compensatory planting works at Location No. 13A (4 nos.)	12	12	17-Feb-11	04-Mar-11	08-Dec-10	23-Dec-10	03	10	17	24
3G1130	Compensatory planting works at Location No. 15 (6 nos. tree pot)	12	12	08-Apr-11	25-Apr-11	27-Jan-11	11-Feb-11	05	12	19	26
Section IV of Works											
Preservation and Protection of Trees											
Preservation and Protection of Existing Trees											
SA-1000	Preservation and protection of trees	602	706	31-Jan-11	22-Jun-11	11-Apr-11	24-Aug-13				
Section V of Works											
Structural Condition Survey in Portion 2, 3A and 3B											
Condition Survey of existing structures											
Condition Survey of existing structures											
SS-1010	Testing for existing structures	60	79	31-Jan-11	10-May-11	07-May-12	08-Aug-12				
Schedule of Milestones											
Schedule of Milestones											
Design of Permanent Works											
CC0200150	2.6-Acceptance of ground investigation reports=1%	0	0	31-Jan-11	31-Jan-11	24-Dec-10	24-Dec-10				
CC0200170	2.8-Acceptance of report on utilities=2%	0	0	31-Jan-11	31-Jan-11	24-Dec-10	24-Dec-10				
CC0200200	2.10-Acceptance of report on construction traffic impact assessment=2%	0	0	31-Jan-11	31-Jan-11	28-Jun-14	28-Jun-14				
CC0200210	2.11-Submission of geotechnical submissions for all permanent geotechnical works=2%	0	0	31-Jan-11	31-Jan-11	25-Aug-14	25-Aug-14				
CC0200220	2.12-Acceptance of geotechnical submissions for all permanent geotechnical works=1%	0	0	31-Jan-11	31-Jan-11	25-Aug-14	25-Aug-14				
CC0200230	2.24-Approval of DDA submission on site investigation works=1%	0	0	31-Jan-11	31-Jan-11	25-Aug-14	25-Aug-14				
CC0200270	2.28-Approval of DDA submission on drainage works=1%	0	0	31-Jan-11	31-Jan-11	25-Aug-14	25-Aug-14				
CC0200390	2.30-Approval of DDA submission on roadworks=2%	0	0	31-Jan-11	31-Jan-11	25-Aug-14	25-Aug-14				
CC0200430	2.34-Approval of DDA submission on provisioning works for TCSS installation=1%	0	0	01-Feb-11	15-Mar-11	25-Aug-14	25-Aug-14				
CC0200470	2.38-Approval of DDA submission on relocation of LRT passenger lift=1%	0	0	15-Mar-11	15-Mar-11	25-Aug-14	25-Aug-14				
Landscape Softworks in Portion 1											
CC0500100	5.1.1 to 5 Trees translocation or felling works in Portion 1	146	101	31-Jan-11	11-May-11	30-Jun-10	05-Aug-11				
Noise Barrier and Noise Enclosure in Portion 2											
CC0900100	9.1-Deliver all the required piling plants on site	0	0	31-Jan-11	31-Jan-11	25-Aug-14	25-Aug-14				
CC0900110	9.2.1 to 20 number of piles of the noise barriers and noise enclosures in Portion 2	724	691	31-Jan-11	21-Dec-12	04-Jan-11	11-Jan-13				
CC0900120	9.4.1 to 10 reinforcement of the pile cap	619	619	19-Apr-11	28-Dec-12	05-Jun-11	19-Jan-13				
CC0900420	9.5.1 to 10 concreting the pile cap	619	619	19-Apr-11	28-Dec-12	05-Jun-11	19-Jan-13				
Reprovision of Yan Oi Bridge											
CC1200100	12.1-On completion of temporary footbridge including foundation works	0	0	20-Apr-11	20-Apr-11	25-Aug-14	25-Aug-14				
Reprovision of Yan Ching Bridge											
CC1300100	13.1.1 to 5 total number of piles of Yan Ching Bridge	57	73	31-Jan-11	13-Apr-11	08-Jan-11	21-Apr-11				
CC1300160	13.3.1 to 5 reinforcement of pile caps of Yan Oi Bridge	37	37	19-Apr-11	25-May-11	21-Apr-11	20-Jun-11				
CC1300210	13.4.1 to 10 concreting the pile cap of Yan Ching Bridge	37	37	19-Apr-11	25-May-11	21-Apr-11	20-Jun-11				
Retaining Wall at Slope No. 6SW-AIFR93											
CC1800100	18.1.1 to 5 Excavation of the Retaining Wall At Slope No. 6SW-AIFR93	23	23	08-Feb-11	02-Mar-11	09-Mar-11	01-Apr-11				
CC1800150	18.2.1 to 5 Formwork of the Retaining Wall At Slope No. 6SW-AIFR93	9	9	15-Mar-11	18-Apr-11	18-Apr-11	27-Apr-11				
CC1800200	18.3.1 to 5 Concreting of the Retaining Wall At Slope No. 6SW-AIFR93	14	14	01-Apr-11	14-Apr-11	09-May-11	16-May-11				
Landscape Softworks in Portion 2											
CC1900100	19.1.1 to 5 Trees translocation or felling works in Portion 2	0	0	01-Feb-11	01-Feb-11	22-Feb-11	10-Mar-11				
Noise Barrier and Noise Enclosure in Portion 3A											
CC2400110	24.2.1 to 20 number of piles of the noise barriers and noise enclosures in Portion 3A	676	676	01-Mar-11	05-Jan-13	02-Mar-11	07-Jan-13				
CC2400320	24.4.1 to 10 reinforcement of the pile cap	672	672	25-Apr-11	25-Feb-13	26-Apr-11	11-Apr-13				
CC2400420	24.5.1 to 10 of concreting the pile cap	672	672	25-Apr-11	25-Feb-13	26-Apr-11	11-Apr-13				

Remaining Level of Effort

3 Months Rolling Programme (cutoff: 31-01-11)

Approved

Actual Work

Actual Level of Effort

Date

Revision

Checked

Approved

07-Feb-11?

Appendix B

**Environmental
Monitoring Programme
in the Reporting Month**

Agreement No. CE 22/2005 (HY) Traffic Improvement to Tuen Mun Road Town Centre Section
Tentative Impact Monitoring Schedule - April 2011 Revision 3

Date		Air Quality 24-hours TSP	Noise L _{Aeq} 30 min	Landscape & Visual	Site Inspection
1-Apr-11	Fri				
2-Apr-11	Sat				
3-Apr-11	Sun				
4-Apr-11	Mon				
5-Apr-11	Tue				
6-Apr-11	Wed				
7-Apr-11	Thu				
8-Apr-11	Fri				
9-Apr-11	Sat				
10-Apr-11	Sun				
11-Apr-11	Mon				
12-Apr-11	Tue				
13-Apr-11	Wed				
14-Apr-11	Thu				SSEMC
15-Apr-11	Fri				
16-Apr-11	Sat				
17-Apr-11	Sun				
18-Apr-11	Mon				
19-Apr-11	Tue				
20-Apr-11	Wed				
21-Apr-11	Thu				
22-Apr-11	Fri				
23-Apr-11	Sat				
24-Apr-11	Sun				
25-Apr-11	Mon				
26-Apr-11	Tue				
27-Apr-11	Wed				
28-Apr-11	Thu				
29-Apr-11	Fri				
30-Apr-11	Sat				

	Public Holiday
	Monitoring Day

Monitoring Details

Monitoring	Quantity	Locations	Parameters
Air Quality	6	Mrs. Aw Boon Haw Secondary School Tai Tung Pui Social Service Building Wu Siu Kui Primary School Choi Cheung Kok Secondary School Tuen Mun Town Hall Yan Oi Tong Community and Sport Centre	24-hour TSP, Wind speed / direction
Noise	6	Kam Fai Garden Tai Tung Pui Social Service Building Yuen Yuen Primary School Wu Siu Kui Primary School Tuen King Building Choi Cheung Kok Secondary School	L _{Aeq} (30 min), L ₁₀ , L ₉₀

Appendix C

**Implementation
Schedule of Mitigation
Measures**

Summary of Implementation Schedule of Mitigation Measures

EIA Ref #	EM&A Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		Noise Control		
3.8.1	2.8.1	<p>Good site practice and management can significantly reduce the noise impact of construction site activities on nearby NSRs</p> <ul style="list-style-type: none"> • only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction works; • machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; • plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs; • mobile plant should be sited as far away from NSRs as possible; and • material stockpiles and other structures should be effectively utilized, where practicable, to screen noise from on-site construction activities. 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>
3.8.4	2.8.3	Use of quieter mechanical equipment	Works Sites / During Construction Phase	✓
3.8.9	2.8.4	<p>Provision of movable noise barrier in the vicinity of the following NSRs</p> <ul style="list-style-type: none"> • FEC (Far East Consortium Tuen Mun Central Building) • FM (Forward Mansion) • HTB (Hing Tai Building) • TMTP1 (Tuen Mun Town Plaza) • WG2 (Waldorf Garden) • CMA (CMA Choi Cheung Kok Secondary School) • LWF (Yan Oi Tong Madam Lau Wong Fat Primary School) • TMF (Tuen Mun Fa Yuen) • LCK (Lui Cheung Kwong Lutheran College) • CLFY1 (Chi Lok Fa Yuen) 	Works Sites from the listed NSRs / During Construction Phase	N/O

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<ul style="list-style-type: none"> TFH (On Ting Estate (Ting Fuk House)) LCKP (Lui Cheung Kwong Lutheran Primary School) TTP (Tung Wah Group of Hospitals Tai Tung Pui Social Service Building) CSBS (CSBS Mrs. Aw Boon Haw Secondary School) KFG3D (Kam Fai Garden) 		
3.8.12	2.8.5	<p>Site clearance and the following activities not to be undertaken in the vicinity of the NSR LCK so as to reduce construction noise impact during normal teaching hours.</p> <ul style="list-style-type: none"> truck would not operate concurrently with other PME's during tree transplanting and noise barrier foundation work. tree transplanting would not be undertaken concurrently with bulk excavation and utilities diversion. construction of storm water drain would not be undertaken concurrently with noise barrier/enclosure foundation. construction of sub-base and road base would not be undertaken concurrently with noise barrier/enclosure installation. road surfacing, construction of road kerbs, central dividers, parapets, and installation of crash cushion and sign gantry would not be undertaken concurrently. installation of gantry and directional lighting, and street lighting would not be undertaken concurrently. 	Work site in the vicinity of Lui Cheung Kwong Lutheran College (LCK) / Stage 2 (Ch. 28050 – 28200 of TMR) during Construction Phase	N/O

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref#	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
3.8.13	2.8.6	Liaise with all the relevant schools to check out their examination periods and activities in the beginning of the work programme in order to make good planning and arrangement of works and provide sufficient mitigation plans to alleviate noise impacts.	CMA Choi Cheung Kok Secondary School (CMA), Yan Oi Tong Madam Lau Wong Fat Primary School (LWF), Lui Cheung Kwong Lutheran College (LCK), Lui Cheung Kwong Lutheran Primary School (LCKP) and CSBS Mrs. Aw Boon Haw Secondary School (CSBS) / During Construction Phase	✓

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<i>Air Quality Control</i>		
4.8.1	3.11.2	<p>Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation.</p> <ul style="list-style-type: none"> • skip hoist for material transport should be totally enclosed by impervious sheeting • every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site • the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores • where a site boundary adjoins a road, streets or other accessible to the public, hording of not less than 2.4m high from ground level should be provided along the entire length except for a 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p> <p>Rdr</p>

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		site entrance or exit <ul style="list-style-type: none"> every stack of more than 20 bags of cement should be covered entirely by impervious sheeting places in an area sheltered on the top and the 3 sides all dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet the height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading the load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise. 		✓ Rdr ✓ ✓ ✓

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		Water Quality Control		
5.8.2	4.3.2	Construction run-off and Drainage <ul style="list-style-type: none"> Silt removal facilities such as silt traps or sedimentation facilities should be provided to remove silt particles from runoff to meet the requirements of the TM standards under the WPCO. The design of silt removal facilities should be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures should be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms. Careful programming of the works to minimise surface excavations for the road improvement works during the wet season. If excavation of soil cannot be avoided during the wet season, exposed slope surfaces should be covered by a tarpaulin or other means. Other measures that need to be implemented before, during, and after rainstorms are summarized in ProPECC PN 1/94. Exposed soil surfaces should be protected by paving or fill material as soon as possible to 	Works Sites / During Construction Phase	✓ ✓ ✓

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<p>reduce the potential of soil erosion.</p> <ul style="list-style-type: none"> Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms. These materials should not be placed near water courses. 		✓
5.8.3 - 5.8.4	4.3.3	<p>General Construction Activities</p> <ul style="list-style-type: none"> Debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering the nearby local stormwater drainage system. Stockpiles of cement and other construction materials should be kept covered when not being used. Oils and fuels should only be used and stored in designated areas which have pollution prevention facilities. All fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event 	Works Sites / During Construction Phase	<p>Obs</p> <p>✓</p> <p>✓</p>
5.8.5	4.3.4	<p>Sewage from Construction Workforce</p> <ul style="list-style-type: none"> Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities 	Works Sites / During Construction Phase	✓

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<i>Waste Management</i>		
6.6.1	5.2.2	<p><i>Good Site Practices</i></p> <ul style="list-style-type: none"> Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site. Training of site personnel in proper waste management and chemical waste handling procedures. Provision of sufficient waste disposal points and regular collection for disposal. Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers. Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites). 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>Obs</p> <p>✓</p>
6.6.5	5.2.6	<p><i>Chemical Wastes</i></p> <ul style="list-style-type: none"> After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals should be collected by a licensed collector for disposal at the CWTC or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation. 	Works Sites / During Construction Phase	<p>Obs</p> <p>✓</p>
6.6.6	5.2.7	<p><i>General Refuse</i></p> <ul style="list-style-type: none"> General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material. 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p>

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
6.6.2	5.2.3	<p><i>Waste Reduction Measures</i></p> <p>Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> • Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal. • Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force. • Any unused chemicals or those with remaining functional capacity shall be recycled. • Use of reusable non-timber formwork to reduce the amount of C&D material. • Prior to disposal of C&D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill. • Proper storage and site practices to minimise the potential for damage or contamination of construction materials. • Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>
6.6.4	5.2.5	<p><i>Construction and Demolition (C&D) Material</i></p> <ul style="list-style-type: none"> • The excavated fill material shall be re-used on-site as backfill material as far as possible. • The surplus excavated material should be disposed of at the designated public fill reception facility, as agreed with the Secretary of the Public Fill Committee, for other beneficial uses. • C&D waste would require disposal to the designated landfill site. • In order to monitor the disposal of C&D materials at the public fill reception facility and landfill and to control fly-tipping, a trip-ticket system should be included. One may make reference to ETWB TCW No. 31/2004 for details. 	Works Sites / During Construction Phase	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		Ecology		
7.9.2	6.2.2	Construction activities should be confined to developed areas of low ecological value, and there should be no direct impact on other habitats within the Study Area.	Works Sites / During Construction Phase	✓
7.9.3	6.2.3	Noise mitigation measures, including installation of noise-emitting construction plant away from egret, careful scheduling of noisy works with high disturbance impact to avoid breeding season of ardeid species (i.e. mid March to August) to prevent impacts on nesting activities of Little Egret, operation of well-maintained machinery, careful programming of works and use of noise reduction facilities could be implemented to mitigate noise impacts arising from construction activities such as road widening and road paving. Temporary noise barrier should also be used to reduce the level of noise during construction. Noise impact would be minimised during operation phase as permanent noise barrier has been proposed to be constructed. The use of low noise road surfacing could also reduce the level of noise during operation.	Works Sites / During Construction Phase	✓
7.9.4	6.2.4	In order to minimise the impact of construction dust to the vegetation and associated wildlife within and around the proposed Works Area, the following mitigation measures should be implemented: <ul style="list-style-type: none"> • regular watering • complete coverage of dusty material storage piles • the use of minimum practical height for dropping excavated material 	Works Sites / During Construction Phase	✓ ✓ ✓
7.9.6	6.2.6	To minimise the indirect impacts to the nearby Tuen Mun River Channel, the following mitigation measures should be implemented: <ul style="list-style-type: none"> • Site runoff could be directed towards regularly cleaned and maintained sand traps, silt traps and where appropriate • Oil/grease separators to minimise risk of sedimentation and pollution to the river channel. • Debris and rubbish generated on-site should be collected, handled and disposed properly. 	Works Sites / During Construction Phase	✓ N/O ✓

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
7.9.5	6.2.5	Standard good site practice measures should be implemented and should include: <ul style="list-style-type: none"> • Placement of equipment in designated Works Areas within the existing disturbed land. • Construction activities should be restricted to the proposed Works Area. • The proposed Works Area should be reinstated immediately after completion of the works. • Open burning on proposed works site is illegal, and will be strictly enforced. • Waste skips should be provided to collect general refuse and construction wastes, which should be disposed regularly and properly off-site. • Soil contaminated by fuel leaked from construction plants should be removed and treated. 	Works Sites / During Construction Phase	✓ ✓ ✓ ✓ ✓ N/O
7.9.7	6.2.7	To minimise the chance of bird collision during operation phase, falcon sticker, tinted materials, embedded opaque stripes and superimposed patterns of thin opaque stripes are methods that could be used during the design of noise barrier.	Works Sites / During Operation Phase	N/O
7.9.8	6.2.8	Compensatory planting is recommended as the current roadside plantation must be removed to give way to the works. Species of choice should be composed of similar native species and the felling and planting ratio should be no less than 1:1 in terms of quantity.	Works Sites / During Operation Phase	N/O

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<i>Landscape and Visual</i>		
Table 8.8	7.3.1	CM1 Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Works Sites / During Construction Phase	✓
Table 8.8	7.3.1	CM2 Existing trees to be retained on site should be carefully protected during construction.		Obs
Table 8.8	7.3.1	CM3 Trees unavoidably affected by the works should be transplanted where practical.		✓
Table 8.8	7.3.1	CM4 Compensatory tree planting should be provided to compensate for felled trees.		✓
Table 8.8	7.3.1	CM5 Control of night-time lighting.		✓
Table 8.8	7.3.1	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.		✓

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Status *
		<i>Land Contamination</i>		
9.8.3	8.2.2	<p>To minimize construction workers' potential contact with the contaminated materials</p> <ul style="list-style-type: none"> • The use of bulk earth-moving excavator equipment would minimise construction workers' potential contact with the contaminated materials; • Exposure to any contaminated materials can be minimised by the wearing of appropriate clothing and personal protective equipment such as gloves (when interacting directly with suspected contaminated material), providing adequate hygiene and washing facilities and preventing smoking and eating during such activities; • Stockpiling of contaminated soil should be avoided as far as possible. If this cannot be avoided, the stockpile of contaminated materials should be segregated from the uncontaminated ones. Moreover, the contaminated materials should be properly covered with waterproof material (e.g. tarpaulin sheet) to avoid leaching of contaminants, especially during rainy season. • Vehicles containing any excavated materials should be suitably covered to limit potential dust emissions or contaminated wastewater run-off, and truck bodies and tailgates should be sealed to prevent any leakage during transport or during wet conditions; • Only licensed waste haulers should be used to collect and transport any contaminated material to an appropriate disposal site and procedures should be developed to ensure that illegal disposal of waste does not occur; • Necessary waste disposal permits should be obtained, as required, from the appropriate authorities, in accordance with the Waste Disposal Ordinance (Cap 354), Waste Disposal (Chemical Waste) (General) Regulation (Cap 35), as required; • Records of the quantities of wastes generated and disposed of should be maintained; Adequate washing facilities should be provided on site; and • In accordance with good construction practice, silt traps should be used to reduce the impact to drainage caused by suspended solids arising from disturbed ground, or any construction materials such as cement and gravel. Groundwater should be disposed of in accordance with the Water Pollution Control Ordinance (Cap 358). 	Excavation zones / During excavation	N/O

All recommendations and requirements resulted during the course of EIA Process, including ACE and / or accepted public comment to the proposed project.

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

Appendix D

Calibration Certificates and Spreadsheets of Air Monitoring Equipments



TISCH ENVIRONMENTAL, INC.
145 SOUTH MIAMI AVE.
VILLAGE OF CLEVELAND, OH 44102
513.467.9000
877.263.7610 TOLL FREE
513.467.9009 FAX
WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Mar 03, 2010 Rootsmeter S/N 9833620 Ta (K) - 292
Operator Tisch Orifice I.D. - 1378 Pa (mm) - 749.3

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.4040	3.2	2.00
2	NA	NA	1.00	0.9880	6.4	4.00
3	NA	NA	1.00	0.8840	8.0	5.00
4	NA	NA	1.00	0.8420	8.8	5.50
5	NA	NA	1.00	0.6950	12.8	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)		Va	(x axis) Qa	(y axis)
1.0019	0.7136	1.4186		0.9957	0.7092	0.8828
0.9976	1.0097	2.0062		0.9915	1.0035	1.2485
0.9953	1.1260	2.2430		0.9892	1.1190	1.3959
0.9943	1.1809	2.3524		0.9882	1.1737	1.4640
0.9890	1.4230	2.8372		0.9829	1.4142	1.7657
Qstd slope (m) = 2.00078				Qa slope (m) = 1.25285		
intercept (b) = -0.01075				intercept (b) = -0.00669		
coefficient (r) = 0.99999				coefficient (r) = 0.99999		
y axis = SQRT[H2O(Pa/760) (298/Ta)]				y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)
Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]
Qa = Va/Time


For subsequent flow rate calculations:

Qstd = 1/m{ [SQRT(H2O(Pa/760) (298/Ta))] - b}
Qa = 1/m{ [SQRT H2O(Ta/Pa)] - b}



TISCH ENVIROMENTAL, INC.
145 SOUTH MIAMI AVE.
VILLAGE OF CLEVES, OH 45002
513.467.9000
877.263.7610 TOLL FREE
513.467.9009 FAX
WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

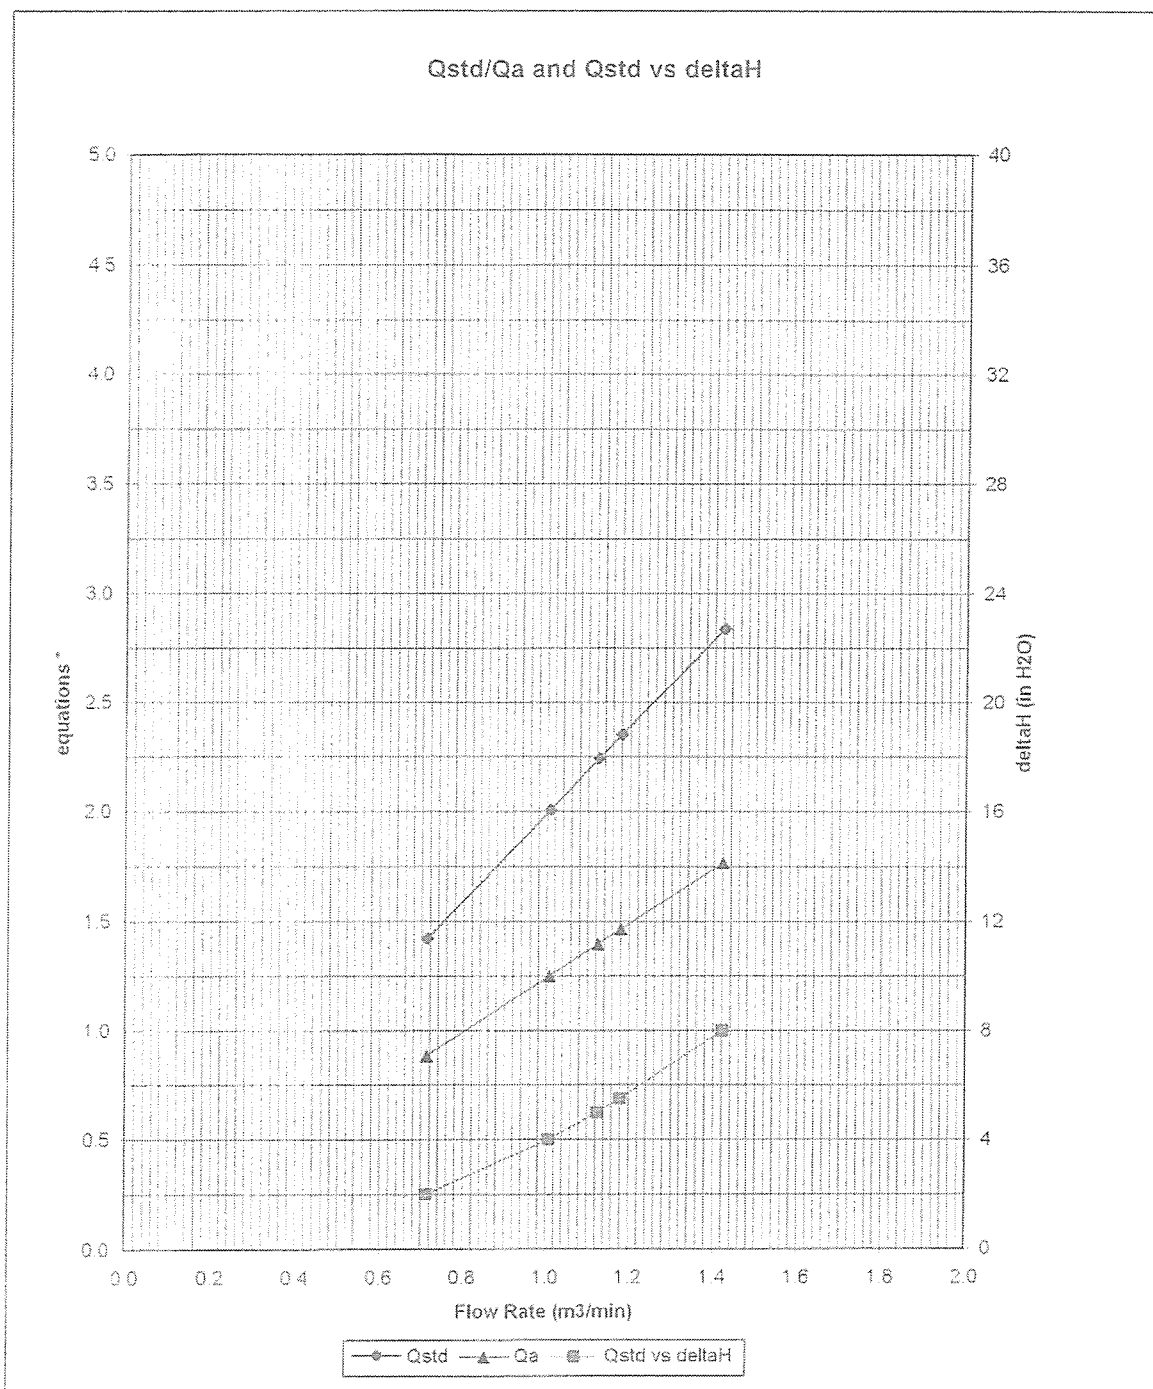

* y-axis equations:

Qstd series:

$$\sqrt{\Delta H \left(\frac{P_a}{P_{std}} \right) \left(\frac{T_{std}}{T_a} \right)}$$

Qa series:

$$\sqrt{\Delta H (T_a / P_a)}$$


#1378

Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-11	Barometric pressure	762 mm Hg
Next Calibration date	31-May-11	Temperature (°C)	20 °C
Sampler location	Tai Tung Pui Social Service	Temperature (K)	293 K
Sampler model	TE-5170	P _{std}	760 mm Hg
Sampler serial number	522	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00078
Intercept of the standard curve, b _s	-0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	2.80	30.00	0.85	30.29
7	4.40	38.00	1.06	38.37
10	7.70	46.00	1.41	46.45
13	9.80	52.00	1.59	52.51
18	11.60	56.00	1.72	56.55

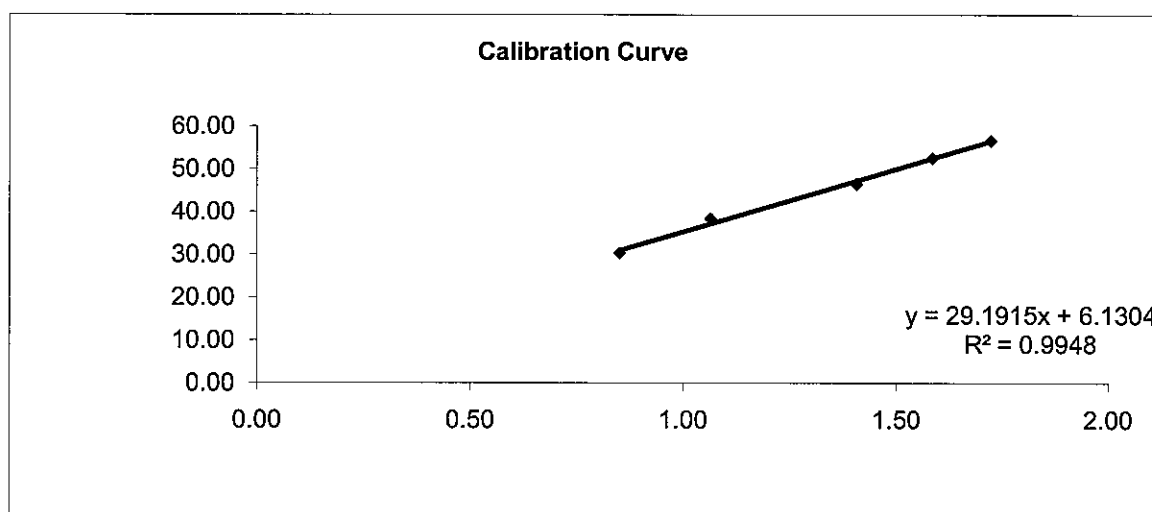

Linear Regression

Sampler slope (m) : **29.1915**
 Sampler intercept (b) : **6.1304**
 Correlation coefficient (R²) : **0.9948**

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____


Date: 1/4/11

Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-11	Barometric pressure	762 mm Hg
Next Calibration date	31-May-11	Temperature (°C)	20 °C
Sampler location	Wu Siu Kui Primary School	Temperature (K)	293 K
Sampler model	TE-5170	P _{std}	760 mm Hg
Sampler serial number	505	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00078
Intercept of the standard curve, b _s	-0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	2.90	30.00	0.86	30.29
7	4.40	36.00	1.06	36.35
10	7.50	46.00	1.39	46.45
13	9.60	52.00	1.57	52.51
18	12.00	60.00	1.75	60.59

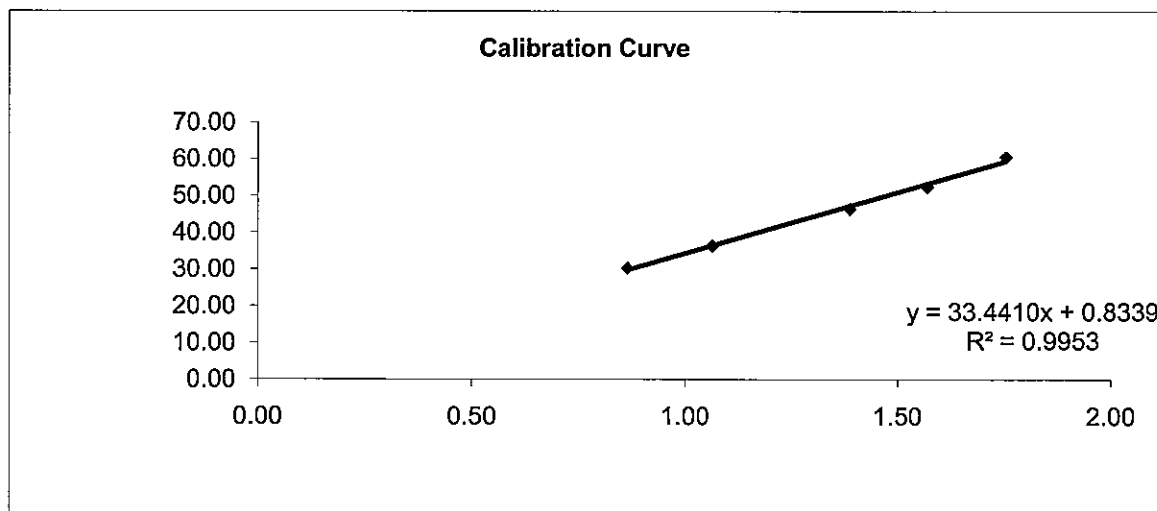

Linear Regression
 Sampler slope (m) : **33.4410**
 Sampler intercept (b) : **0.8339**
 Correlation coefficient (R²) : **0.9953**

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____


Date: 1/4/11

Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-11	Barometric pressure	762 mm Hg
Next Calibration date	31-May-11	Temperature (°C)	20 °C
Sampler location	Choi Cheung Kok Secondary	Temperature (K)	293 K
Sampler model	Thermo Anderson	P _{std}	760 mm Hg
Sampler serial number	1278	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00078
Intercept of the standard curve, b _s	-0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	3.00	30.00	0.88	30.29
7	4.70	39.00	1.10	39.38
10	7.60	48.00	1.40	48.47
13	10.60	54.00	1.65	54.53
18	12.80	60.00	1.81	60.59

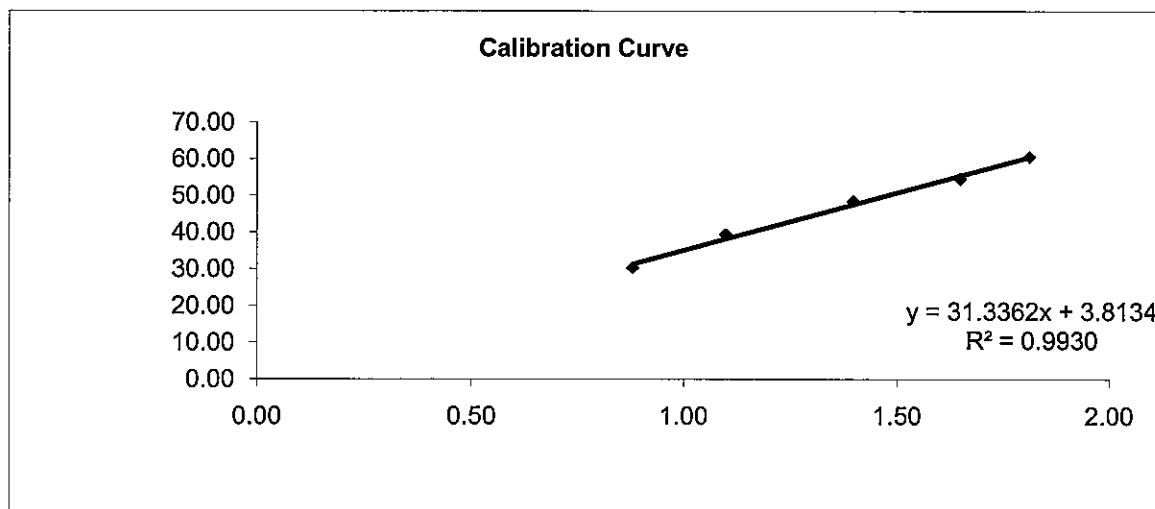

Linear Regression

Sampler slope (m) :	31.3362
Sampler intercept (b) :	3.8134
Correlation coefficient (R ²) :	0.9930

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____


Date: 1/4/11

Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-11	Barometric pressure	762 mm Hg
Next Calibration date	31-May-11	Temperature (°C)	20 °C
Sampler location	Tuen Mun Town Hall	Temperature (K)	293 K
Sampler model	TE-5170	P _{std}	760 mm Hg
Sampler serial number	516	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00078
Intercept of the standard curve, b _s	-0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	3.20	32.00	0.91	32.31
7	4.40	38.00	1.06	38.37
10	7.60	46.00	1.40	46.45
13	9.60	53.00	1.57	53.52
18	11.60	56.00	1.72	56.55

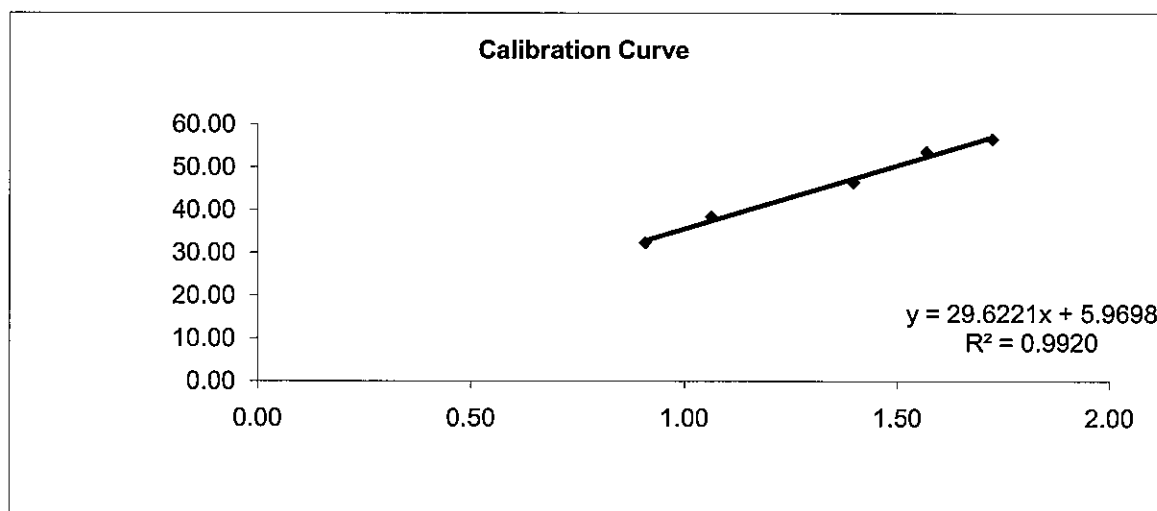

Linear Regression

Sampler slope (m) :	29.6221
Sampler intercept (b) :	5.9698
Correlation coefficient (R ²) :	0.9920

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____

Date: 1/4/11


Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date 1-Apr-11
 Next Calibration date 31-May-11
 Sampler location Yan Oi Tong
 Sampler model TE-5170
 Sampler serial number 510

Barometric pressure 762 mm Hg
 Temperature (°C) 20 °C
 Temperature (K) 293 K
 P_{std} 760 mm Hg
 T_{std} 298 K

Calibrator model GMW-2535
 Calibrator serial number 1378
 Slope of the standard curve, m_s 2.00078
 Intercept of the standard curve, b_s -0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q_{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	3.20	30.00	0.91	30.29
7	4.80	38.00	1.11	38.37
10	8.00	46.00	1.43	46.45
13	10.20	54.00	1.62	54.53
18	12.40	60.00	1.78	60.59

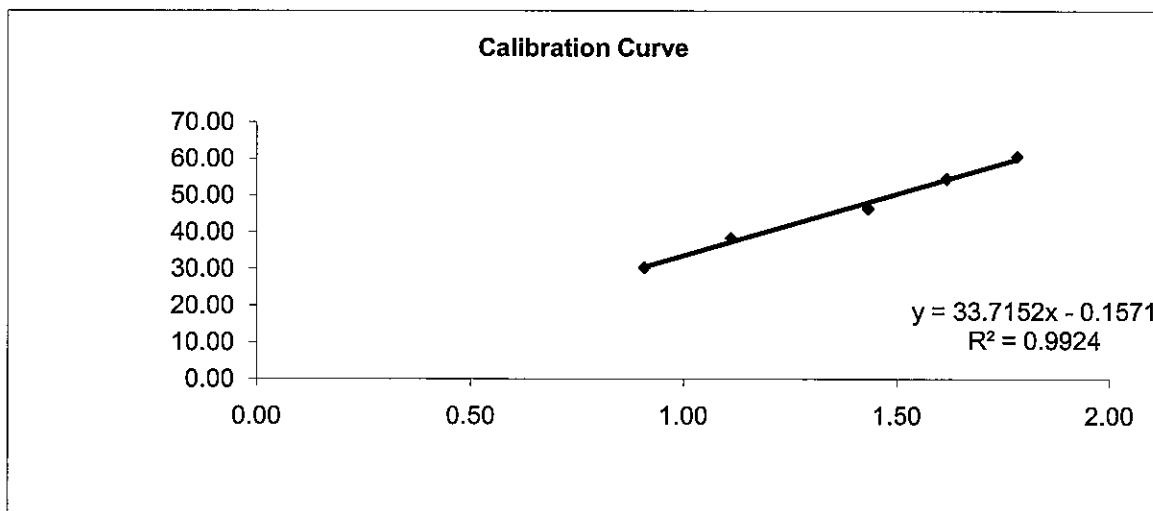

Linear Regression

Sampler slope (m) : 33.7152
 Sampler intercept (b) : -0.1571
 Correlation coefficient (R^2) : 0.9924

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____


Date: 1/4/11

Ove Arup Partners Hong Kong Limited
High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-11	Barometric pressure	762 mm Hg
Next Calibration date	31-May-11	Tempature (°C)	20 °C
Sampler location	Mrs. AW Boon Haw Secondary School	Tempature (K)	293 K
Sampler model	TE-5170	P _{std}	760 mm Hg
Sampler serial number	521	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00078
Intercept of the standard curve, b _s	-0.01075

Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	2.90	32.00	0.86	32.31
7	4.20	38.00	1.04	38.37
10	7.60	46.00	1.40	46.45
13	10.20	54.00	1.62	54.53
18	11.60	58.00	1.72	58.57

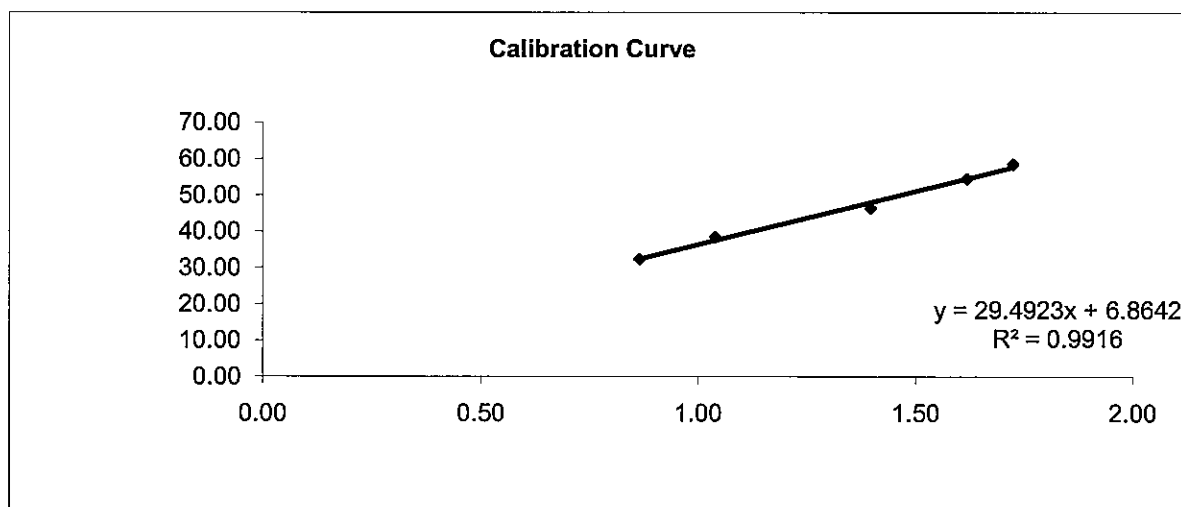

Linear Regression

Sampler slope (m) : **29.4923**
 Sampler intercept (b) : **6.8642**
 Correlation coefficient (R²) : **0.9916**

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: _____

Date: 1/4/2011

Checked by: _____

Date: 1/4/11

Appendix E

**Impact Air Quality
Monitoring Results**

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Mrs Aw Boon Haw Secondary School (AM1) - 24 hour TSP

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time (mins.)	Total vol. (m³)	(ug/m³) AM1
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130320	Apr-11	1-Apr-11	AM1	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7923	2.9189	0.1266	1.4793	1.4712	1.48	10969.30	10993.30	1440.0	2124.36	59.6
130326	Apr-11	6-Apr-11	AM1	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7953	2.7653	0.1056	1.7211	1.713	1.72	10993.30	11017.30	1440.0	2472.54	49.6
130332	Apr-11	11-Apr-11	AM1	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7983	2.6117	0.1462	1.9629	1.9548	1.96	11017.30	11041.30	1440.0	2820.72	69.0
130338	Apr-11	16-Apr-11	AM1	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8013	2.4581	0.0803	2.2047	2.1966	2.20	11041.30	11065.30	1440.0	3168.90	38.2
130344	Apr-11	20-Apr-11	AM1	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8043	2.3045	0.2143	2.4465	2.4384	2.44	11065.30	11089.30	1440.0	3517.08	101.1
130350	Apr-11	26-Apr-11	AM1	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8073	2.1509	0.0921	2.6883	2.6802	2.68	11089.30	11113.30	1440.0	3865.26	43.8
130357	Apr-11	30-Apr-11	AM1	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8103	1.9973	0.1030	2.9301	2.922	2.93	11113.30	11137.30	1440.0	4213.44	49.0

Average (ug/m³)	58.6
Max (ug/m³)	101.1
Min (ug/m³)	38.2

Action Level (ug/m³)	146
Limit Level (ug/m³)	260

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Tai Tung Pui Social Service Building (AM2) - 24 hour TSP

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time	Total vol. (m³)	(ug/m³) AM2
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130321	Apr-11	1-Apr-11	AM2	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7928	2.8933	0.1005	1.5196	1.5115	1.52	5123.10	5147.10	1440.0	2182.39	46.1
130327	Apr-11	6-Apr-11	AM2	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7958	2.7397	0.1146	1.7614	1.7533	1.76	5147.10	5171.10	1440.0	2530.57	52.4
130333	Apr-11	11-Apr-11	AM2	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7988	2.5861	0.0846	2.0032	1.9951	2.00	5171.10	5195.10	1440.0	2878.75	38.9
130339	Apr-11	16-Apr-11	AM2	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8018	2.4325	0.1329	2.245	2.2369	2.24	5195.10	5219.10	1440.0	3226.93	61.5
130345	Apr-11	20-Apr-11	AM2	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8048	2.2789	0.2031	2.4868	2.4787	2.48	5219.10	5243.10	1440.0	3575.11	93.2
130351	Apr-11	26-Apr-11	AM2	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8078	2.1253	0.0871	2.7286	2.7205	2.72	5243.10	5267.10	1440.0	3923.29	40.3
130358	Apr-11	30-Apr-11	AM2	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8108	1.9717	0.0866	2.9704	2.9623	2.97	5267.10	5291.10	1440.0	4271.47	40.1

Average (ug/m³)	53.2
Max (ug/m³)	93.2
Min (ug/m³)	38.9

Action Level (ug/m³)	151
Limit Level (ug/m³)	260

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Wu Siu Kui Primary School (AM3) - 24 hour TSP

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time	Total vol. (m³)	(ug/m³) AM3
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130322	Apr-11	1-Apr-11	AM3	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7933	2.8677	0.0749	1.5599	1.5518	1.56	9289.39	9313.39	1440.0	2240.42	35.1
130328	Apr-11	6-Apr-11	AM3	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7963	2.7141	0.1447	1.8017	1.7936	1.80	9313.39	9337.39	1440.0	2588.60	67.7
130334	Apr-11	11-Apr-11	AM3	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7993	2.5605	0.1069	2.0435	2.0354	2.04	9337.39	9361.39	1440.0	2936.78	50.2
130340	Apr-11	16-Apr-11	AM3	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8023	2.4069	0.1644	2.2853	2.2772	2.28	9361.39	9385.39	1440.0	3284.96	77.8
130346	Apr-11	20-Apr-11	AM3	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8053	2.2533	0.0745	2.5271	2.519	2.52	9385.39	9409.39	1440.0	3633.14	35.0
130352	Apr-11	26-Apr-11	AM3	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8083	2.0997	0.1555	2.7689	2.7608	2.76	9409.39	9433.39	1440.0	3981.32	73.6
130316	Apr-11	30-Apr-11	AM3	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.8113	1.9461	0.2801	3.0107	3.0026	3.01	9433.39	9457.39	1440.0	4329.50	132.5

Average (ug/m³)	67.4
Max (ug/m³)	132.5
Min (ug/m³)	35.0

Action Level (ug/m³)	150
Limit Level (ug/m³)	260

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Choi Cheung Kok Secondary School (AM4) - 24 hour TSP

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time	Total vol. (m³)	(ug/m³) AM4
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130323	Apr-11	1-Apr-11	AM4	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7764	2.8901	0.1137	1.4896	1.482	1.49	10171.12	10195.12	1440.0	2139.55	53.1
130329	Apr-11	6-Apr-11	AM4	Fine	Normal Operation	763.0	762.0	19.0	21.0	50.0	50.0	2.782	2.9494	0.1674	1.4933	1.4868	1.49	10195.12	10219.12	1440.0	2145.67	78.0
130335	Apr-11	11-Apr-11	AM4	Fine	Normal Operation	761.0	762.0	23.0	22.0	50.0	50.0	2.7948	2.8801	0.0853	1.4804	1.4841	1.48	10219.12	10243.12	1440.0	2134.44	40.0
130341	Apr-11	16-Apr-11	AM4	Fine	Normal Operation	757.0	756.0	25.0	24.0	50.0	50.0	2.7915	2.9436	0.1521	1.4708	1.4724	1.47	10243.12	10267.12	1440.0	2119.10	71.8
130347	Apr-11	20-Apr-11	AM4	Fine	Normal Operation	762.0	760.0	21.0	23.0	50.0	50.0	2.789	2.8897	0.1007	1.4868	1.4793	1.48	10267.12	10291.12	1440.0	2135.59	47.2
130353	Apr-11	26-Apr-11	AM4	Fine	Normal Operation	757.0	755.0	24.0	25.0	50.0	50.0	2.7882	2.9085	0.1203	1.4735	1.4686	1.47	10291.12	10315.12	1440.0	2118.31	56.8
130359	Apr-11	30-Apr-11	AM4	Fine	Normal Operation	757.0	755.0	24.0	25.0	50.0	50.0	2.7872	2.8417	0.0545	1.4735	1.4686	1.47	10315.12	10339.12	1440.0	2118.31	25.7

Average (ug/m³)	53.2
Max (ug/m³)	78.0
Min (ug/m³)	25.7

Action Level (ug/m³)	150
Limit Level (ug/m³)	260

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Tuen Mun Town Hall (AM5) - 24 hour TSP

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time (mins.)	Total vol. (m³)	(ug/m³) AM5
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130324	Apr-11	1-Apr-11	AM5	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7878	2.8575	0.0697	1.503	1.495	1.50	9957.27	9981.27	1440.0	2158.56	32.3
130330	Apr-11	6-Apr-11	AM5	Fine	Normal Operation	763.0	762.0	19.0	21.0	50.0	50.0	2.7697	2.8842	0.1145	1.5069	1.500	1.50	9981.27	10005.27	1440.0	2164.97	52.9
130336	Apr-11	11-Apr-11	AM5	Fine	Normal Operation	761.0	762.0	23.0	22.0	50.0	50.0	2.7852	2.8416	0.0564	1.4932	1.4972	1.50	10005.27	10029.27	1440.0	2153.09	26.2
130342	Apr-11	16-Apr-11	AM5	Fine	Normal Operation	757.0	756.0	25.0	24.0	50.0	50.0	2.7961	2.9646	0.1685	1.4831	1.4848	1.48	10029.27	10053.27	1440.0	2136.89	78.9
130348	Apr-11	20-Apr-11	AM5	Fine	Normal Operation	762.0	760.0	21.0	23.0	50.0	50.0	2.7706	2.8851	0.1145	1.500	1.4921	1.50	10053.27	10077.27	1440.0	2154.31	53.1
130354	Apr-11	26-Apr-11	AM5	Fine	Normal Operation	757.0	755.0	24.0	25.0	50.0	50.0	2.7876	2.9331	0.1455	1.486	1.4808	1.48	10077.27	10101.27	1440.0	2136.10	68.1
130315	Apr-11	30-Apr-11	AM5	Fine	Normal Operation	757.0	755.0	24.0	25.0	50.0	50.0	2.8009	3.001	0.2001	1.486	1.4808	1.48	10101.27	10125.27	1440.0	2136.10	93.7




Average (ug/m³)	57.9
Max (ug/m³)	93.7
Min (ug/m³)	26.2
Action Level (ug/m³)	146
Limit Level (ug/m³)	260




Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Impact Air Quality Monitoring Result at Yan Oi Tong Community and Sports Centre (AM6) - 24 hour TSP




Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m³/min)		Average Flow Rate (m³/min)	Elapse Time		Sampling Time	Total vol. (m³)	(ug/m³) AM6
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish			
130325	Apr-11	1-Apr-11	AM6	Fine	Normal Operation	762.0	760.0	20.0	22.0	50.0	50.0	2.7844	2.8788	0.0944	1.5022	1.4952	1.50	6290.80	6314.80	1440.0	2158.13	43.7
130331	Apr-11	6-Apr-11	AM6	Fine	Normal Operation	763.0	762.0	19.0	21.0	50.0	50.0	2.782	2.8904	0.1084	1.5057	1.4997	1.50	6314.80	6338.80	1440.0	2163.89	50.1
130337	Apr-11	11-Apr-11	AM6	Fine	Normal Operation	761.0	762.0	23.0	22.0	50.0	50.0	2.7848	2.8814	0.0966	1.4937	1.4972	1.50	6338.80	6362.80	1440.0	2153.45	44.9
130343	Apr-11	16-Apr-11	AM6	Fine	Normal Operation	757.0	756.0	25.0	24.0	50.0	50.0	2.7898	2.968	0.1782	1.4848	1.4862	1.49	6362.80	6386.80	1440.0	2139.12	83.3
130349	Apr-11	20-Apr-11	AM6	Fine	Normal Operation	762.0	760.0	21.0	23.0	50.0	50.0	2.7773	2.8735	0.0962	1.4997	1.4927	1.50	6386.80	6410.80	1440.0	2154.53	44.7
130356	Apr-11	26-Apr-11	AM6	Fine	Normal Operation	757.0	755.0	24.0	25.0	50.0	50.0	2.777	2.8668	0.0898	1.4873	1.4828	1.49	6410.80	6434.80	1440.0	2138.47	42.0
130360	Apr-11	30-Apr-11	AM6	Fine	Normal Operation	757.0	755.0	24.0	25.0	50.0	50.0	2.7837	2.9237	0.1400	1.4873	1.4828	1.49	6434.80	6458.80	1440.0	2138.47	65.5




Average (ug/m³)	53.5
Max (ug/m³)	83.3
Min (ug/m³)	42.0

Action Level (ug/m³)	147
Limit Level (ug/m³)	260

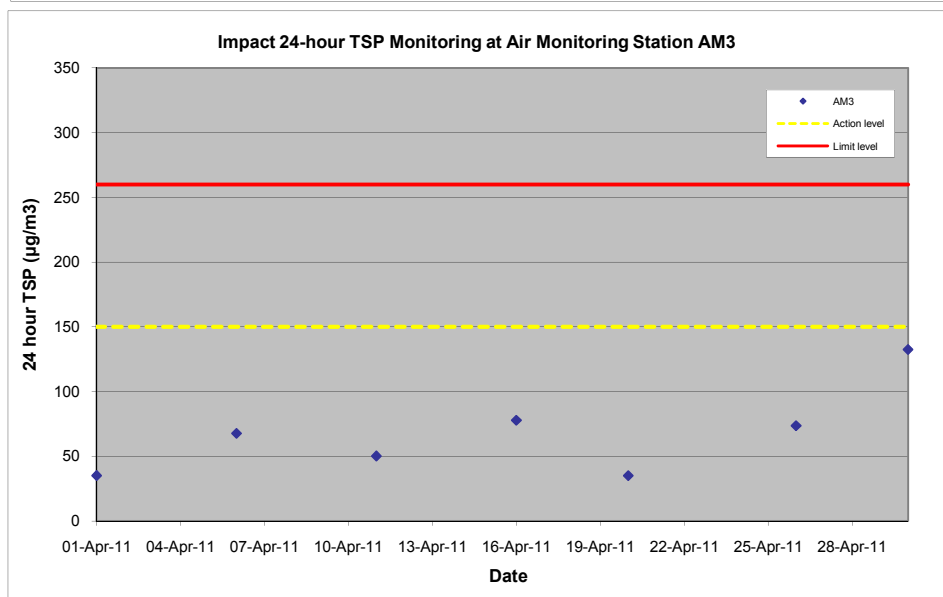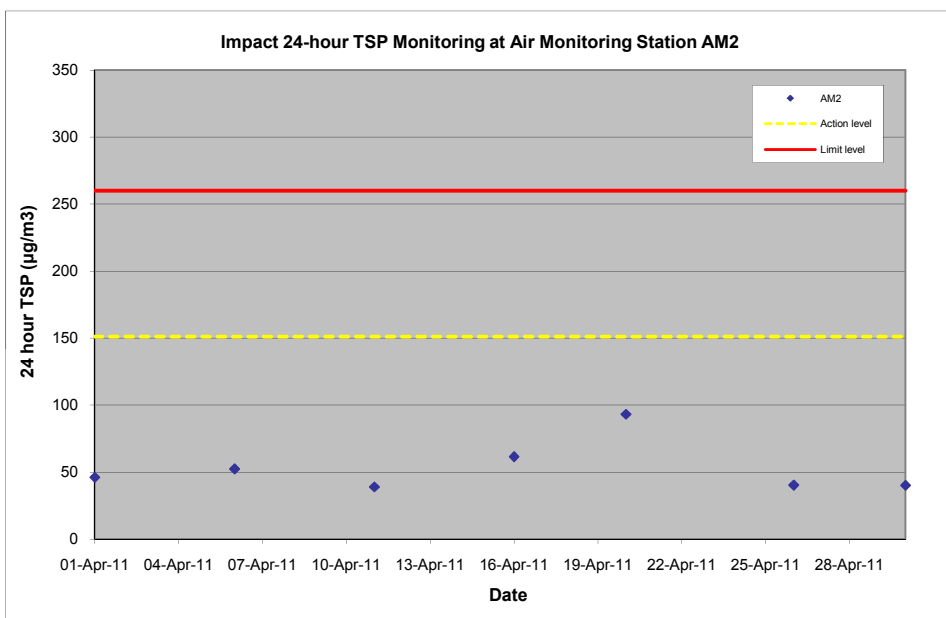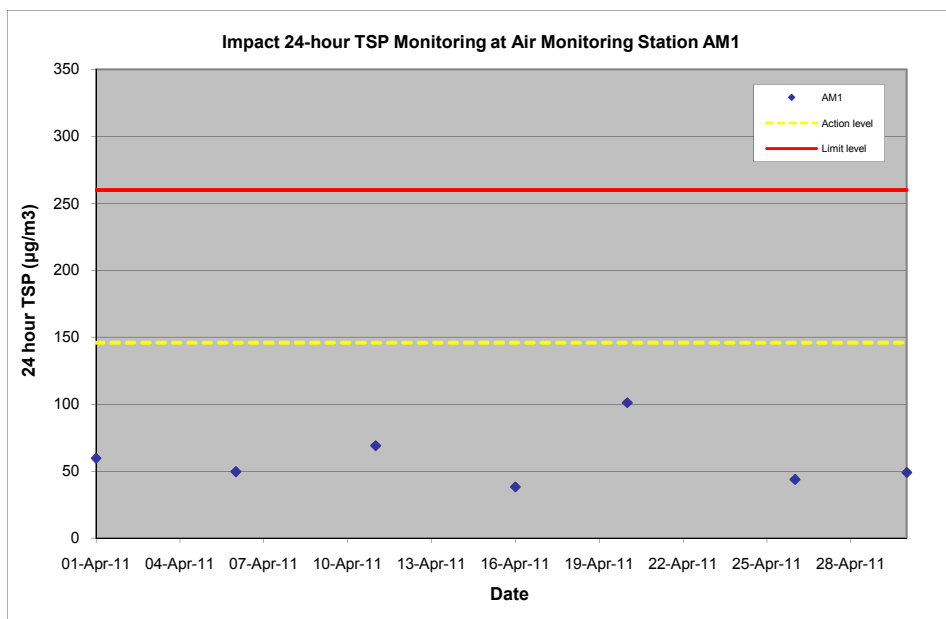

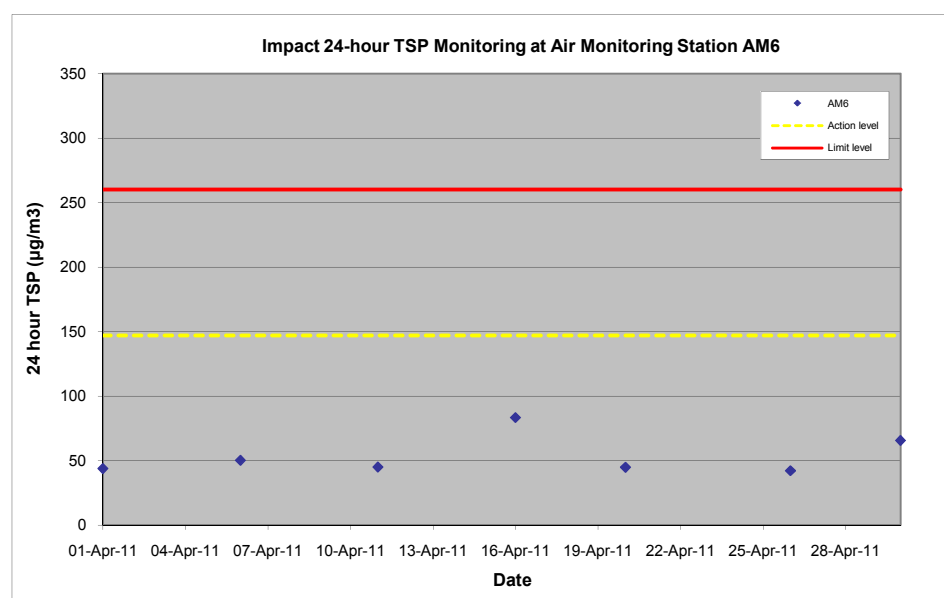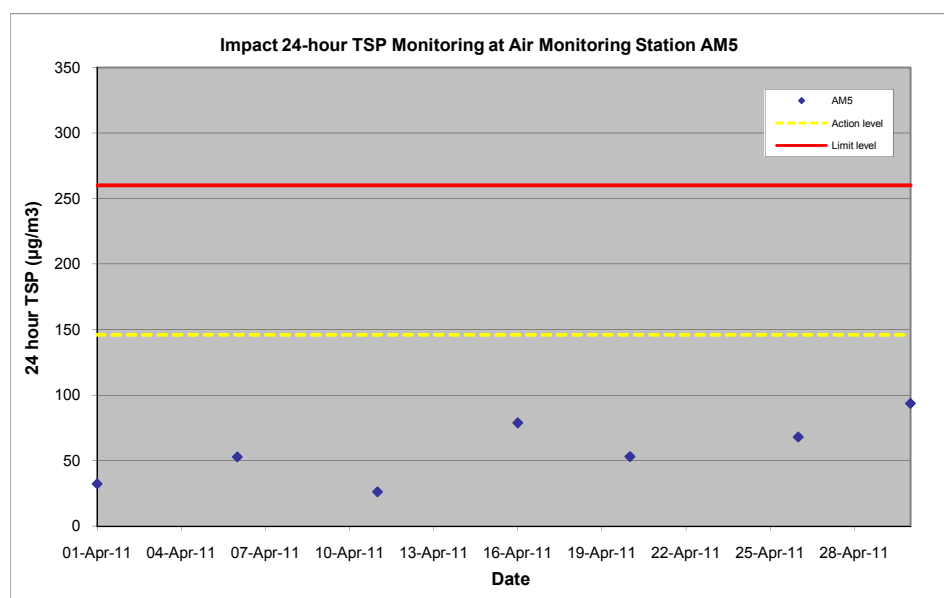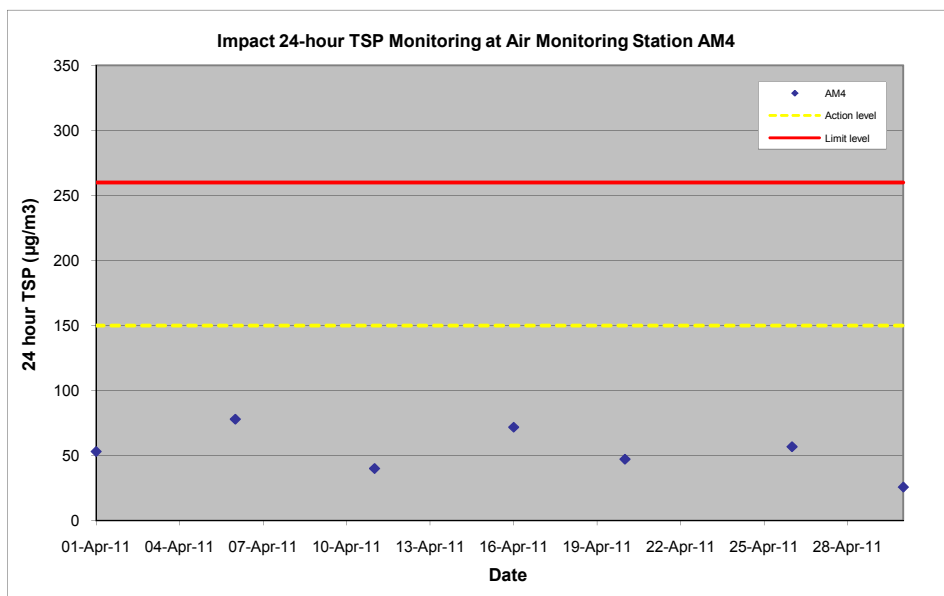


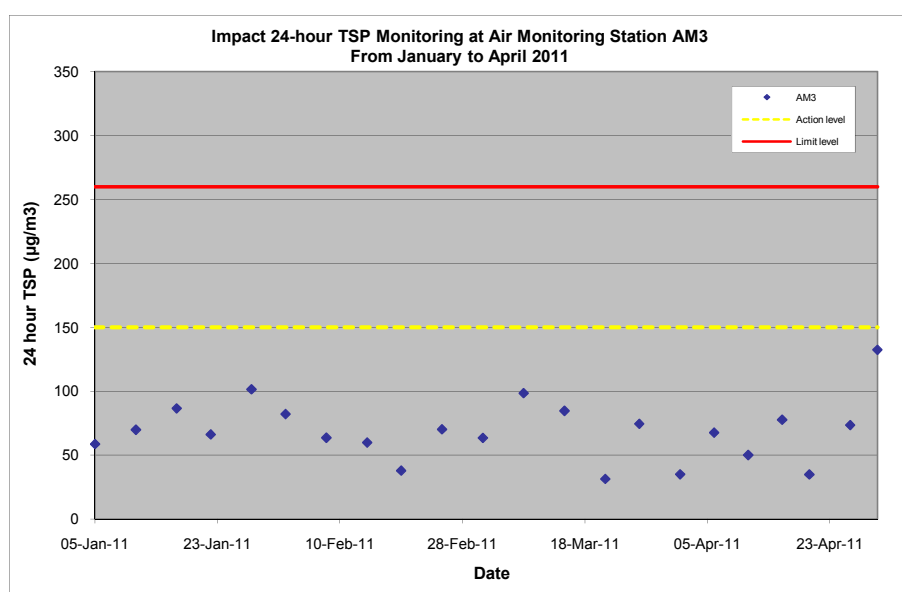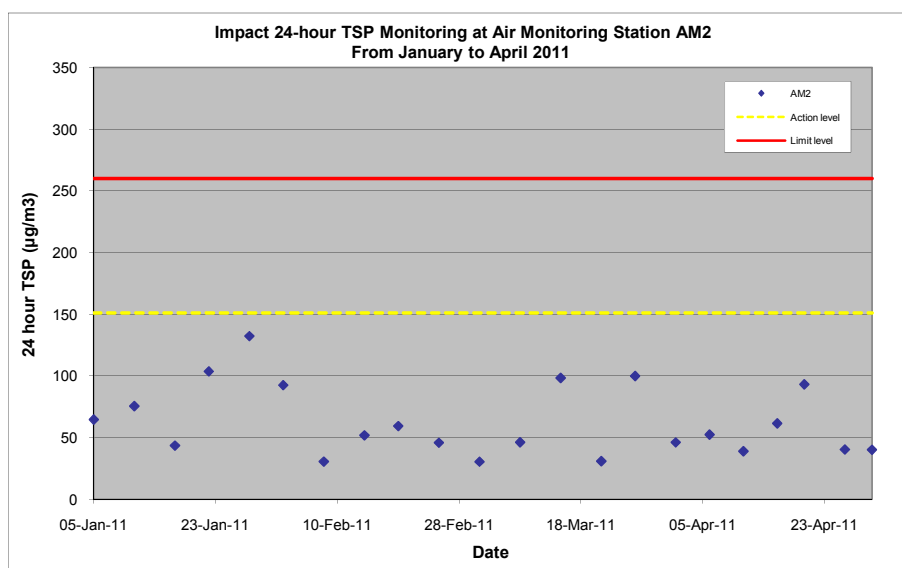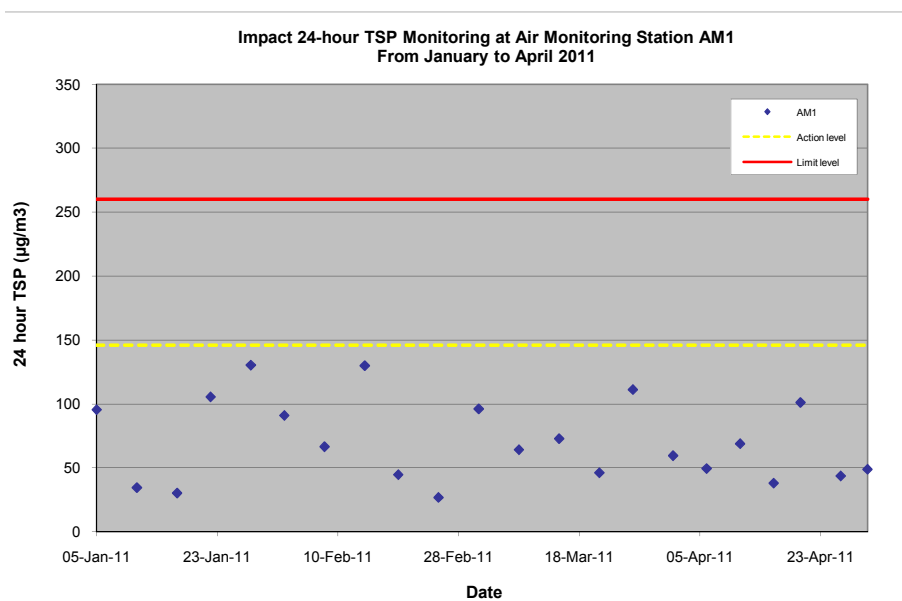


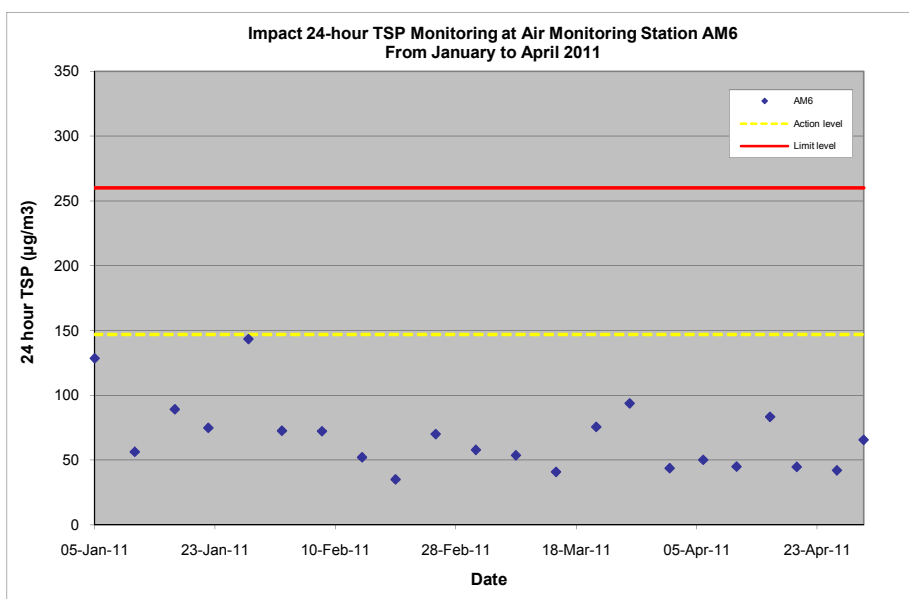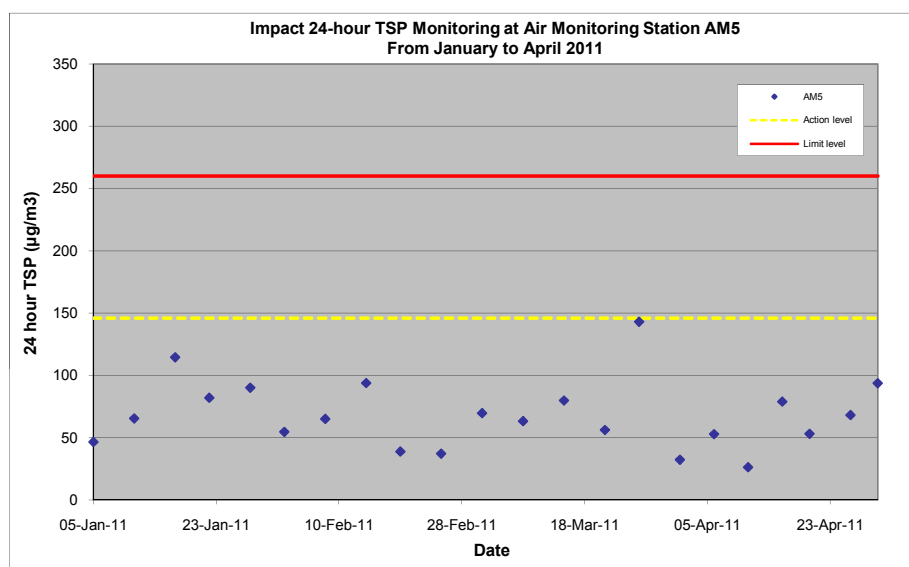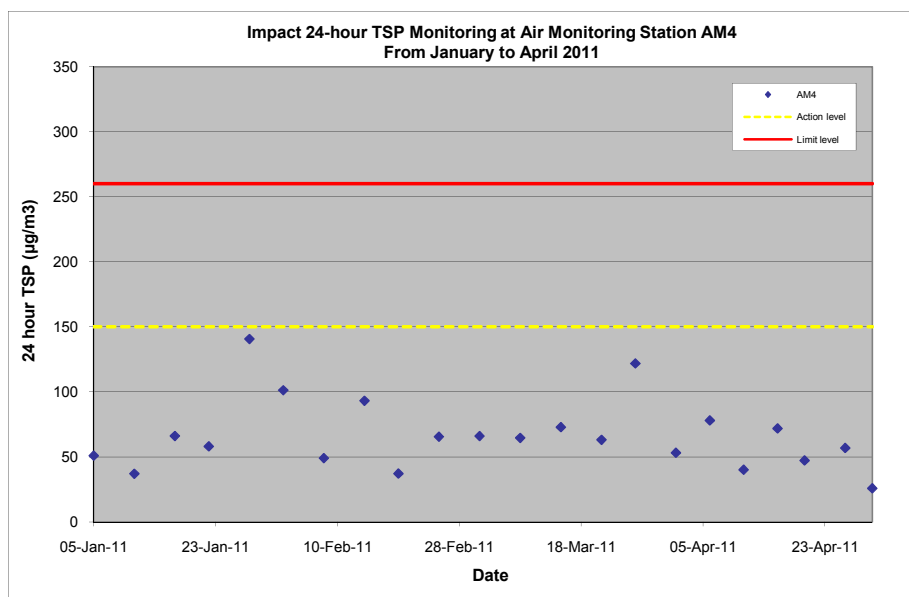

Appendix F

Wind Data

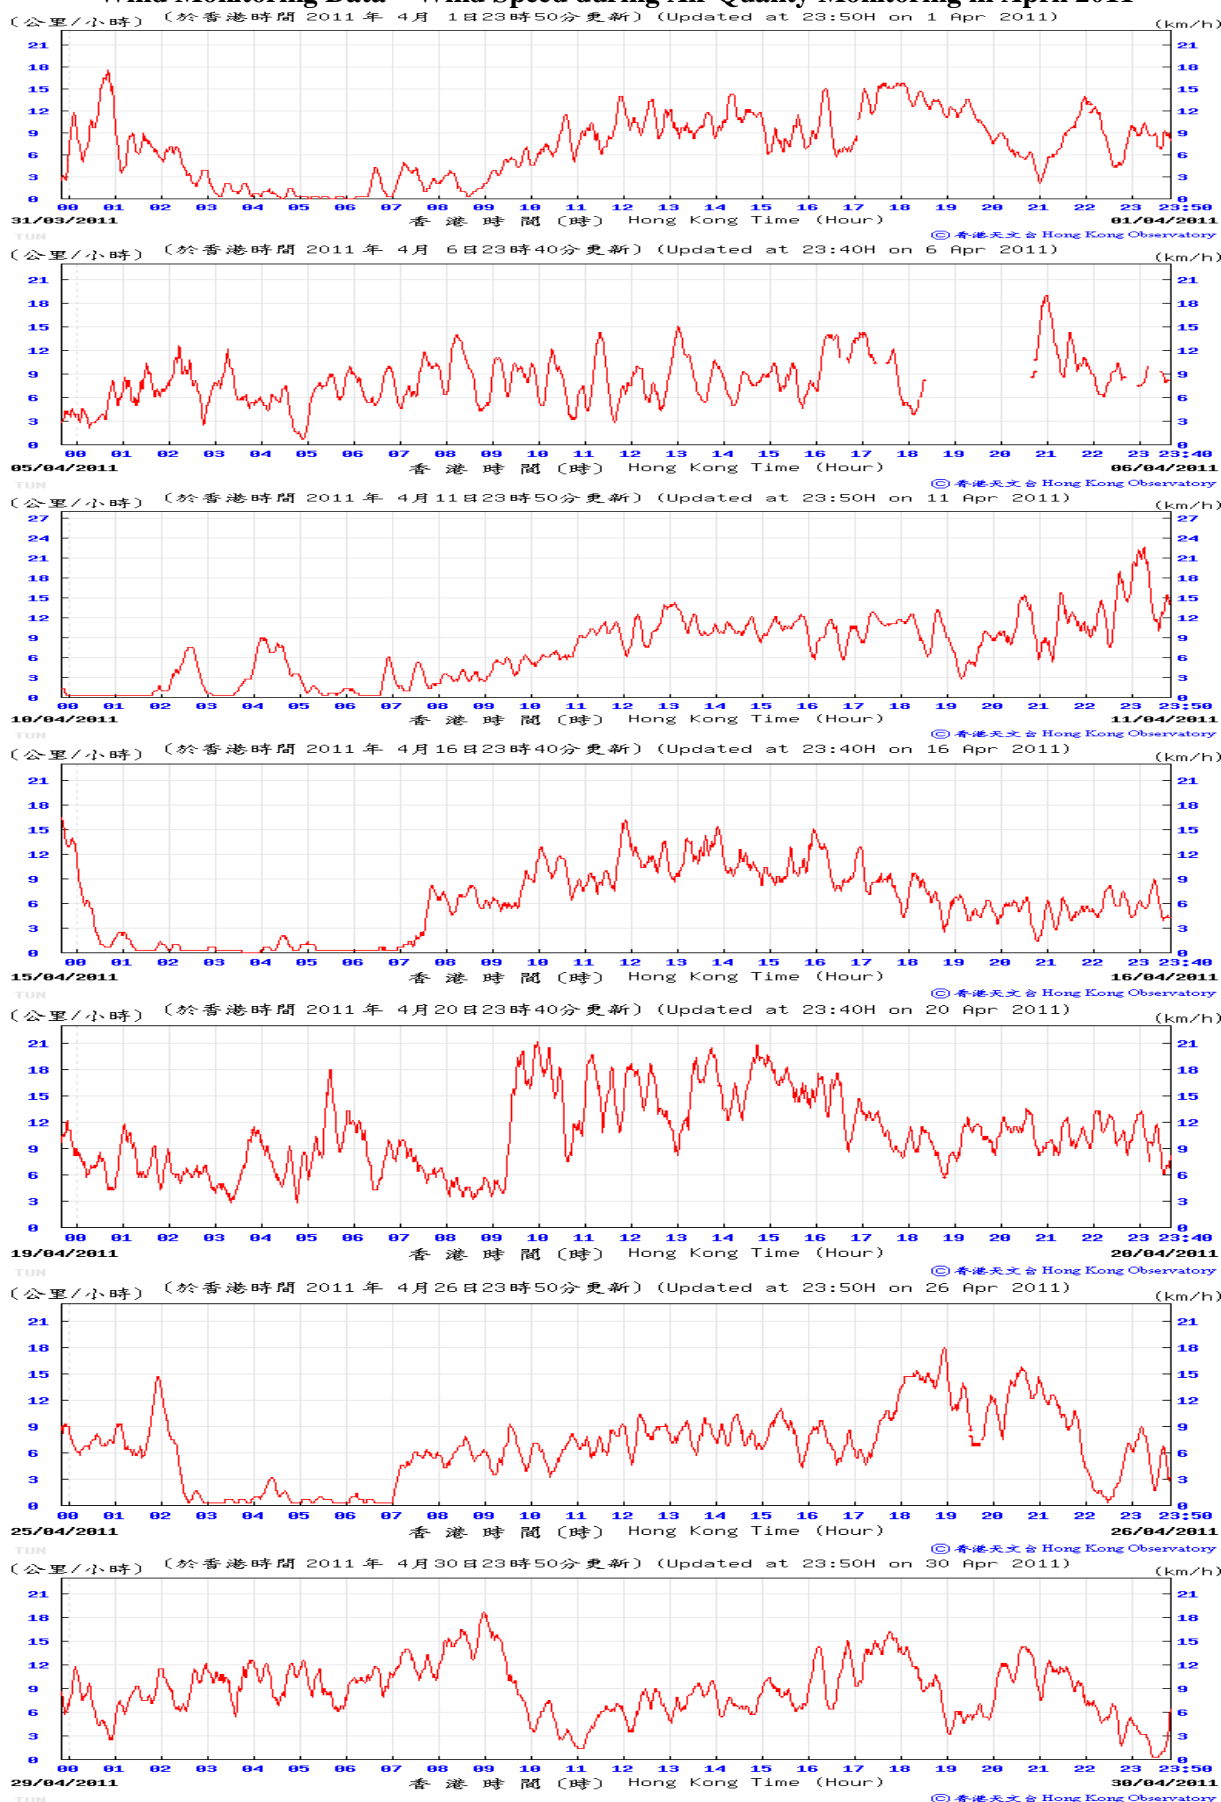Wind Monitoring Data – Wind Speed during Air Quality Monitoring in April 2011

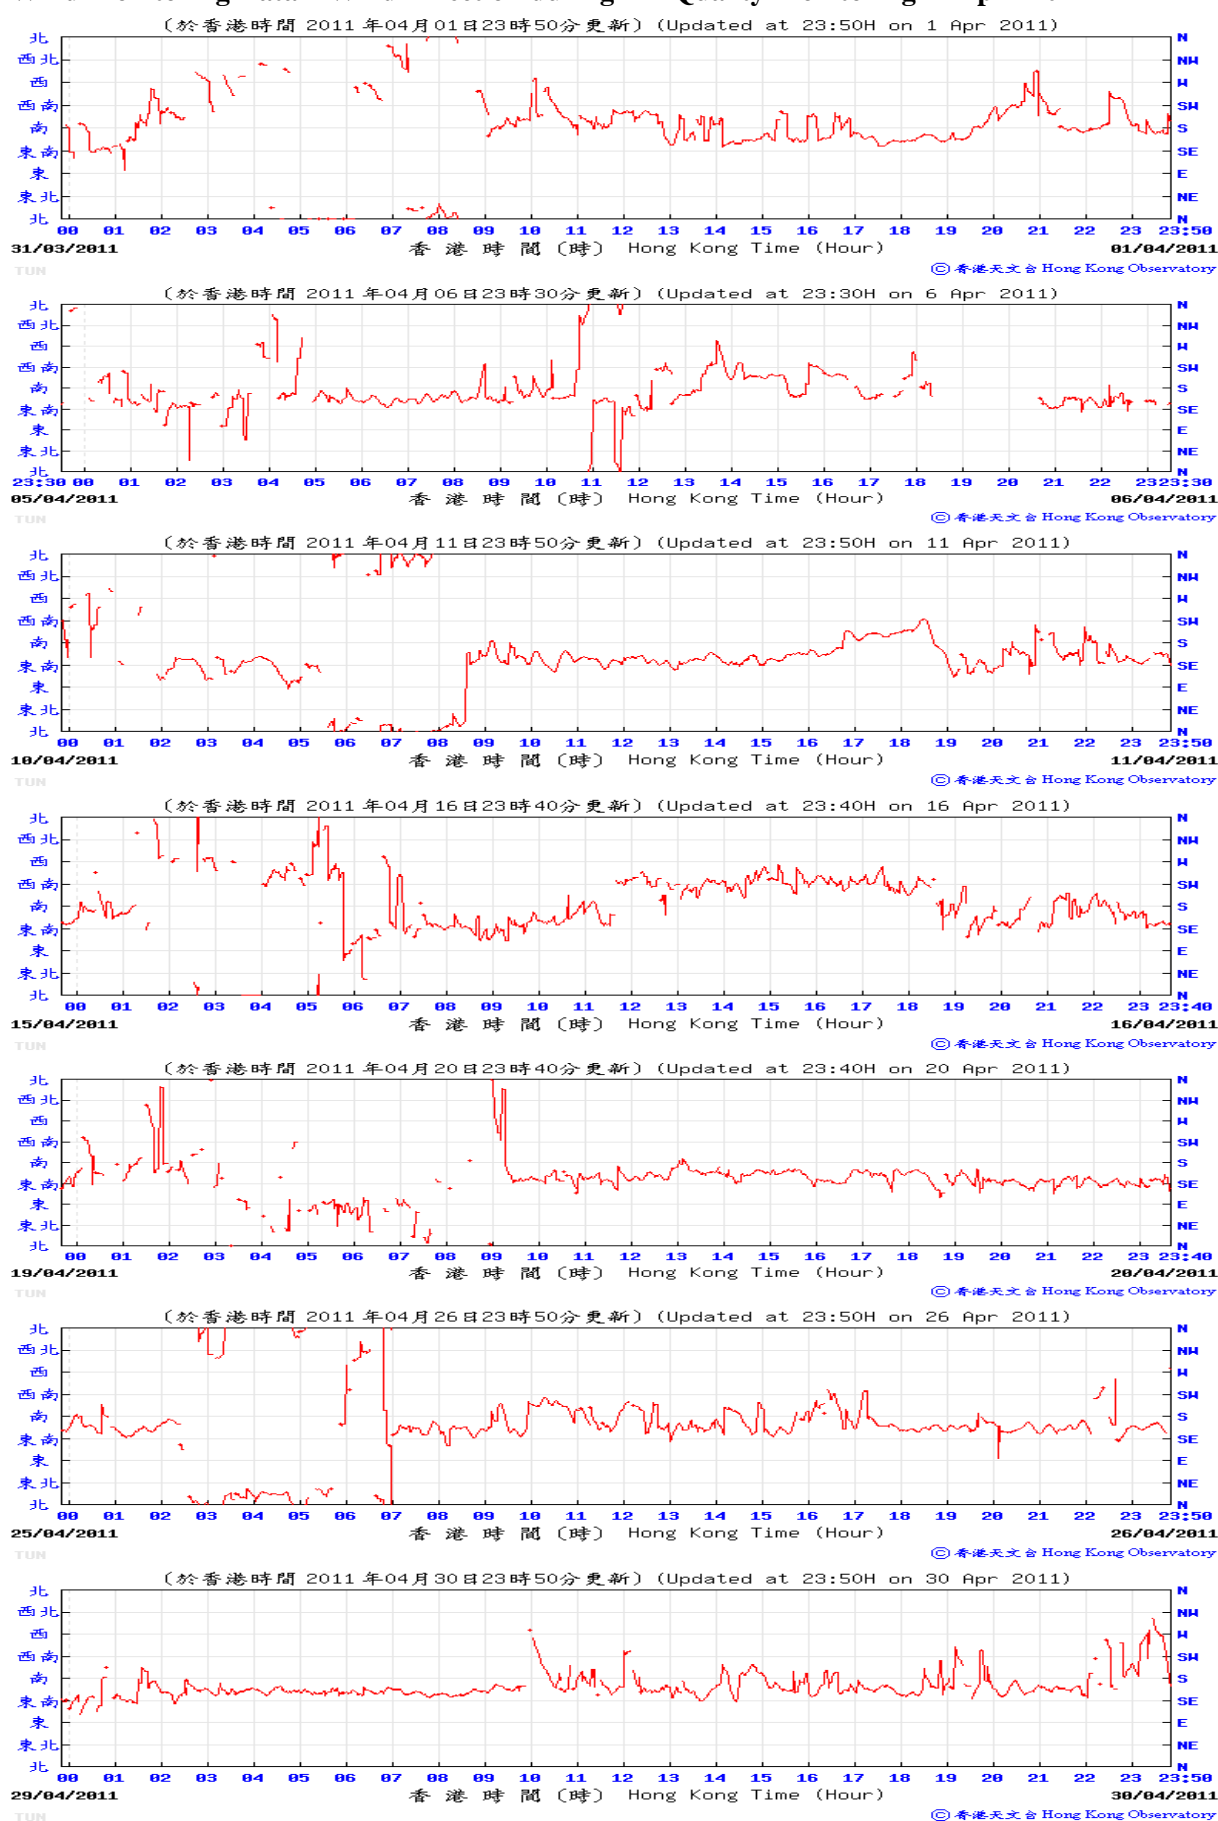Wind Monitoring Data – Wind Direction during Air Quality Monitoring in April 2011

Appendix G

**Calibration Certificates
of Noise Monitoring
Equipments**

CERTIFICATE OF CALIBRATION

Issued by: Brüel & Kjær UK Ltd.

Date of Issue: 10 NOV 2009 Certificate Number: 17957



0174

Brüel & Kjær 

Bedford House, Rutherford Close, Stevenage.
Hertfordshire. SG1 2ND
Telephone: 01438 739100 Fax.: 01438 739199
E-Mail : ukservice@bksv.com

Page 1 of 4 pages

Approved signatory

Name: S. TILAHUN

Signature: 

CALIBRATION OF MULTI FREQUENCY CALBRATOR TYPE 4226 ("Free Field and Random" version)

Client: ARUP ACOUSTICS
PARKIN HOUSE
8 ST THOMAS STREET, WINCHESTER
HANTS SO23 9HE

Calibrator Type 4226, S/No: 1531372

With Coupler UA0915, S/No: 1531372

Client Inventory Number: —

Manufacturer: Brüel & Kjær

Equipment Received on: 13 OCT 2009

Calibration Date: 10 NOV 2009

Brüel & Kjær Reference No: 1-192904717

Measurement Method

The Calibration was performed to Laboratory Procedure TWI-103.

Sound pressure level in the 1/2 inch coupler of the calibrator was measured with a laboratory grade condenser microphone Type 4180, used as a working standard, calibrated by the National Physical Laboratory.

This certificate is issued in accordance with the laboratory accreditation requirements of the United Kingdom Accreditation Service. It provides traceability of measurement to recognised national standards, and to units of measurement realised at the National Physical Laboratory or other recognised national standards laboratories. This certificate may not be reproduced other than in full, except with the prior written approval of the issuing laboratory.

CERTIFICATE OF CALIBRATION

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

17957

Page 2 of 4 pages

The measured sound pressure was compared with that generated in the coupler of a working standard pistonphone calibrated by the National Physical Laboratory whose output was cross checked against a reference standard pistonphone, also calibrated by the National Physical Laboratory, using the same microphone and at the same ambient conditions. Appropriate corrections for atmospheric pressure conditions during calibration and for the measurement frequency and level response were taken into account.

Sound pressure level results are the mean of 5 measurements.

Results apply directly to the following settings on the calibrator, pressure, linear, calibration, 94dB, microphone group a, b, c.

Results for frequency and distortion are the result of a single measurement.

Results for 104 and 114dB are only at 125Hz, 1kHz and 8kHz, compared with the output at 94dB.

Calibration results apply at ambient conditions during the process of calibration.

Calibrations marked (Not UKAS Accredited) in this certificate have been included for completeness.

CALIBRATION RESULTS

4226 Settings: Linear, Pressure, 94dB, Microphone Group c.

Frequency Setting Hz	Sound Pressure Level in dB re 20µPa	Frequency Hz (Not UKAS Accredited)	Distortion % (Not UKAS Accredited)
31.5	94.15	31.63	0.5
63	94.13	63.13	0.2
125	94.09	125.9	0.1
250	94.06	251.3	0.1
500	94.04	502.5	0.1
1k	94.08	1.005k	0.1
2k	94.04	1.979k	0.3
4k	94.04	3.957k	0.7
8k	94.21	7.915k	0.2
12.5k	94.12	12.66k	0.2

CERTIFICATE OF CALIBRATION

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

17957

Page 3 of 4 pages

Expanded uncertainty of calibration:

Sound Pressure Level: $\pm 0.15\text{dB}$ from 31.5Hz to 2kHz,
 $\pm 0.20\text{dB}$ at 4kHz and 8kHz,
 $\pm 0.25\text{dB}$ at 12.5kHz
Frequency: ± 1 last significant digit reported.
Distortion: $\pm 0.3\%$ distortion.

The reported expanded uncertainty is based on a standard uncertainty multiplied by a coverage factor $k=2$, providing a level of confidence of approximately 95%. The uncertainty evaluation has been carried out in accordance with UKAS requirements.

ADDITIONAL TESTS

Sound Pressure Levels at Settings of 94, 104 and 114 dB

Frequency	Difference 104-94dB	Difference 114-94dB
125 Hz	9.99	19.97
1kHz	10.00	19.98
8kHz	9.96	19.94

Result of a single measurement, expanded uncertainty $\pm 0.15\text{dB}$

Inverted "A" Weighting, Readings Relative to 1kHz in dB

Frequency Hz	31.5	63	125	250	500	1 k	2 k	4 k	8 k	12.5 k
Target Value	+ 39.4	+ 26.2	+ 16.1	+ 8.6	+ 3.2	0	- 1.2	- 1.0	+ 1.1	+ 4.3
Reading	39.6	26.2	16.1	8.6	3.2	0.0	-1.2	-0.9	1.3	4.4

Target values according to BS EN 60651 - 1994 - results of a single measurement, values rounded to 0.1 dB, expanded uncertainty $\pm 0.3\text{dB}$.

CERTIFICATE OF CALIBRATION

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

17957
Page 4 of 4 pages

Free Field and Random settings

	Free Field Setting						Random	
	Microphone Group a		Microphone Group b		Microphone Group c		Microphone Group b	
Freq. Hz	Target Value dB	Reading dB	Target Value dB	Reading dB	Target Value dB	Reading dB	Target Value dB	Reading dB
250	0	0.00	0	0.00	0	0.00	0	0.00
500	0	0.00	0	0.00	0	0.00	0	0.00
1k	+0.15	0.14	+0.20	0.19	+0.10	0.08	+0.05	0.03
2k	+0.50	0.48	+0.45	0.43	+0.35	0.34	+0.10	0.08
4k	+1.35	1.33	+1.05	1.03	+0.95	0.93	+0.15	0.13
8k	+4.50	4.46	+2.80	2.77	+2.60	2.58	+0.40	0.38
12.5k	+7.35	7.28	+5.60	5.54	+5.05	5.00	+1.50	1.48

Target values as specified in the manufacturer's manual, result of a single measurement, expanded uncertainty $\pm 0.2\text{dB}$.

Ambient conditions during calibration were:

Atmospheric Pressure 100.7 kPa

Temperature 24 °C

Relative Humidity 47 %

Checked by:



Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2010001

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2320707
Brüel & Kjær ½ " Microphone Kit	4188	2630746

Date of Test: 20 July 2010

Carried out by: Jacky Chan

Approved by: William Ng

Signature:



Signature:



Ambient Conditions During Test

Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372

Certificate of Calibration Serial No.	17957
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009
UKAS Accredited Calibration Laboratory No.	07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2010002

Tel: +852 2268 3216

Fax: +852 2268 3950


CERTIFICATE OF CONFORMITY


<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2654435
Brüel & Kjær ½ " Microphone Kit	4188	2658546

Date of Test: 20 July 2010

Carried out by: Jacky Chan

Approved by: William Ng

Signature: 

Signature: 

Ambient Conditions During Test

Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372

Certificate of Calibration Serial No.	17957
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009
UKAS Accredited Calibration Laboratory No.	07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2010003

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2320694
Brüel & Kjær ½ " Microphone Kit	4188	2641132

Date of Test: 20 July 2010


Carried out by: Jacky Chan

Approved by: William Ng

Signature:



Signature:



Ambient Conditions During Test

Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372

Certificate of Calibration Serial No.	17957
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009
UKAS Accredited Calibration Laboratory No.	07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAC Certificate No. 2010004

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY


<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2654436
Brüel & Kjær ½ " Microphone Kit	4188	2658547

Date of Test: 20 July 2010


Carried out by: Jacky Chan

Approved by: William Ng

Signature:



Signature:



Ambient Conditions During Test

Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372

Certificate of Calibration Serial No. 17957
By Brüel & Kjær (UK) Ltd Calibration Date: 10 November 2009
UKAS Accredited Calibration Laboratory No. 07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2010005

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2562763
Brüel & Kjær ½ " Microphone Kit	4188	2658559

Date of Test: 20 July 2010


Carried out by: Jacky Chan

Approved by: William Ng

Signature:



Signature:



Ambient Conditions During Test

Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372

Certificate of Calibration Serial No.	17957
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009
UKAS Accredited Calibration Laboratory No.	07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAC Certificate No. 2010006

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Sound Level Meter Kit	2238	2320696
Brüel & Kjær ½ " Microphone Kit	4188	2630747

Date of Test: 20 July 2010


Carried out by: Jacky Chan

Approved by: William Ng

Signature:



Signature:



Ambient Conditions During Test	
Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372
Certificate of Calibration Serial No.	17957	
By Brüel & Kjær (UK) Ltd Calibration Date:	10 November 2009	
UKAS Accredited Calibration Laboratory No.	07174	

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2010021

Tel: +852 2268 3216

Fax: +852 2268 3950

CERTIFICATE OF CONFORMITY

Description of Test Instrument
RION NC-74 Acoustic Calibrator

Type No
NC-74


Serial No
34304660

Date of Test: 20 July 2010


Carried out by: Jacky Chan

Approved by: William Ng

Signature:



Signature:



Ambient Conditions During Test	
Atmospheric Pressure:	1KPa
Air Temperature:	22°C
Relative Humidity:	60%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

Description of Reference Calibrator

Type No

Serial No

Brüel & Kjær Multi Frequency Calibrator
Brüel & Kjær Coupler

4226
UA0915

1531372
1531372

Certificate of Calibration Serial No.

17957

By Brüel & Kjær (UK) Ltd Calibration Date:

10 November 2009

NAMAS Accredited Calibration Laboratory No.

07174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Appendix H

**Impact Noise
Monitoring Results**

Agreement No. 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section - Environmental Team
Day-time Noise Monitoring Results - 2 April 2011

ID	Premise	Time	Measured Noise Level, dB(A)				Baseline Noise Level, dB(A)	Construction Noise Level, dB(A)
			L _{Aeq} 30min	Limit	L ₁₀ 5min	L ₉₀ 5min	L _{Aeq} 30min	L _{Aeq} 30min
N1	Kam Fai Garden	09:50 - 10:20	77	75	82	75	76	72
N2	Tai Tung Pui Social Service Building	10:10 - 10:40	77	75	79	74	78	Measured ≤ Baseline
N3	Yuen Yuen Primary School	11:20 - 11:50	66	70	67	65	69	Measured ≤ Baseline
N4	Wu Siu Kui Primary School	08:30 - 09:00	66	70	66	64	67	Measured ≤ Baseline
N5	Tuen King Building	13:00 - 13:30	70	75	71	67	70	Measured ≤ Baseline
N6	Choi Cheung kok Secondary School	14:00 - 14:30	68	70	70	66	69	Measured ≤ Baseline

Note: (#): Construction Noise Level = Measured Noise Level - Baseline Noise Level

Agreement No. 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section - Environmental Team
Day-time Noise Monitoring Results - 7 April 2011

ID	Premise	Time	Measured Noise Level, dB(A)				Baseline Noise Level, dB(A)	Construction Noise Level, dB(A)
			L _{Aeq} 30min	Limit	L ₁₀ 5min	L ₉₀ 5min	L _{Aeq} 30min	L _{Aeq} 30min
N1	Kam Fai Garden	09:45 - 10:15	73	75	75	72	76	Measured ≤ Baseline
N2	Tai Tung Pui Social Service Building	10:30 - 11:00	73	75	74	71	78	Measured ≤ Baseline
N3	Yuen Yuen Primary School	11:15 - 11:45	66	70	68	65	69	Measured ≤ Baseline
N4	Wu Siu Kui Primary School	08:30 - 09:00	65	70	66	63	67	Measured ≤ Baseline
N5	Tuen King Building	13:00 - 13:30	70	75	72	68	70	Measured ≤ Baseline
N6	Choi Cheung kok Secondary School	13:50 - 14:20	70	70	72	67	69	59

Note: (#): Construction Noise Level = Measured Noise Level - Baseline Noise Level

Agreement No. 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section - Environmental Team
Day-time Noise Monitoring Results - 12 April 2011

ID	Premise	Time	Measured Noise Level, dB(A)				Baseline Noise Level, dB(A)	Construction Noise Level, dB(A)
			L _{Aeq} 30min	Limit	L ₁₀ 5min	L ₉₀ 5min	L _{Aeq} 30min	L _{Aeq} 30min
N1	Kam Fai Garden	09:45 - 10:15	78	75	81	75	76	73
N2	Tai Tung Pui Social Service Building	10:30 - 11:00	78	75	80	76	78	Measured ≤ Baseline
N3	Yuen Yuen Primary School	11:05 - 11:35	66	70	69	65	69	Measured ≤ Baseline
N4	Wu Siu Kui Primary School	08:30 - 09:00	67	70	70	65	67	Measured ≤ Baseline
N5	Tuen King Building	13:00 - 13:30	71	75	72	68	70	62
N6	Choi Cheung kok Secondary School	13:50 - 14:20	69	70	71	67	69	Measured ≤ Baseline

Note: (#): Construction Noise Level = Measured Noise Level - Baseline Noise Level

Agreement No. 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section - Environmental Team
Day-time Noise Monitoring Results - 21 April 2011


ID	Premise	Time	Measured Noise Level, dB(A)				Baseline Noise Level, dB(A)	Construction Noise Level, dB(A)
			L _{Aeq} 30min	Limit	L ₁₀ 5min	L ₉₀ 5min	L _{Aeq} 30min	L _{Aeq} 30min
N1	Kam Fai Garden	09:45 - 10:15	75	75	77	73	76	Measured ≤ Baseline
N2	Tai Tung Pui Social Service Building	10:30 - 11:00	76	75	79	74	78	Measured ≤ Baseline
N3	Yuen Yuen Primary School	11:05 - 11:35	68	70	69	66	69	Measured ≤ Baseline
N4	Wu Siu Kui Primary School	08:30 - 09:00	67	70	69	65	67	Measured ≤ Baseline
N5	Tuen King Building	13:15 - 13:45	70	75	72	68	70	Measured ≤ Baseline
N6	Choi Cheung kok Secondary School	14:00 - 14:30	69	70	71	68	69	Measured ≤ Baseline

Note: (#): Construction Noise Level = Measured Noise Level - Baseline Noise Level


Agreement No. 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section - Environmental Team
Day-time Noise Monitoring Results - 27 April 2011

ID	Premise	Time	Measured Noise Level, dB(A)				Baseline Noise Level, dB(A)	Construction Noise Level, dB(A)
			L _{Aeq} 30min	Limit	L ₁₀ 5min	L ₉₀ 5min	L _{Aeq} 30min	L _{Aeq} 30min
N1	Kam Fai Garden	10:45 - 11:15	78	75	81	75	76	74
N2	Tai Tung Pui Social Service Building	11:30 - 12:00	77	75	79	74	78	Measured ≤ Baseline
N3	Yuen Yuen Primary School	13:00 - 13:30	69	70	70	67	69	Measured ≤ Baseline
N4	Wu Siu Kui Primary School	11:30 - 12:00	67	70	69	66	67	Measured ≤ Baseline
N5	Tuen King Building	13:50 - 14:20	72	75	73	70	70	66
N6	Choi Cheung kok Secondary School	14:30 - 15:00	70	70	72	69	69	64


Note: (#): Construction Noise Level = Measured Noise Level - Baseline Noise Level

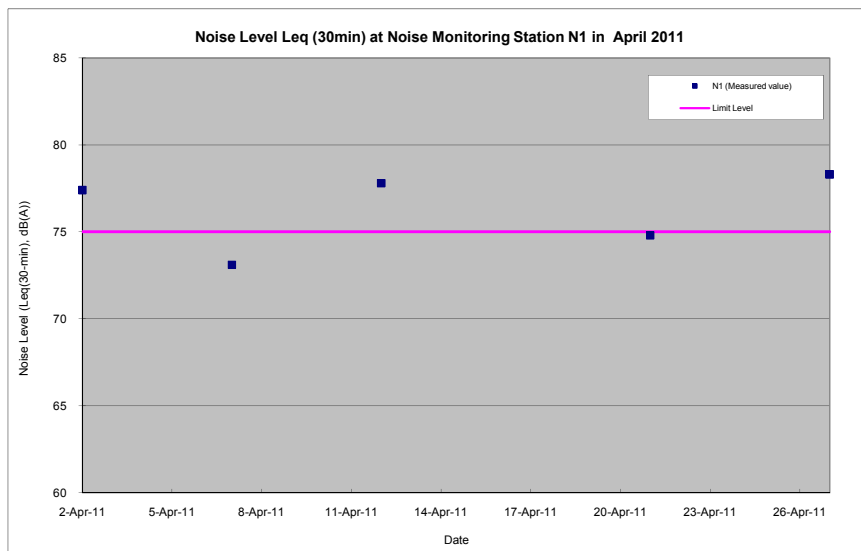




Note: For compliance comparison, please refer to above table and report.

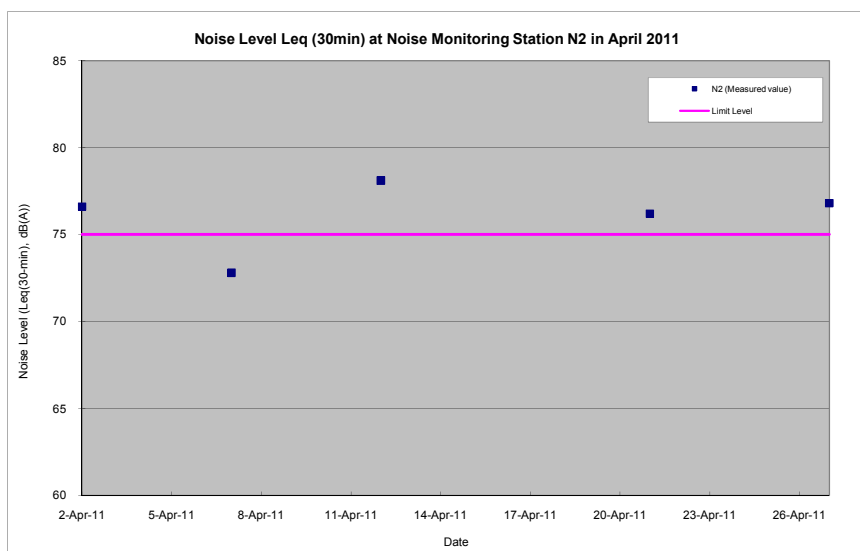


Note: For compliance comparison, please refer to above table and report.

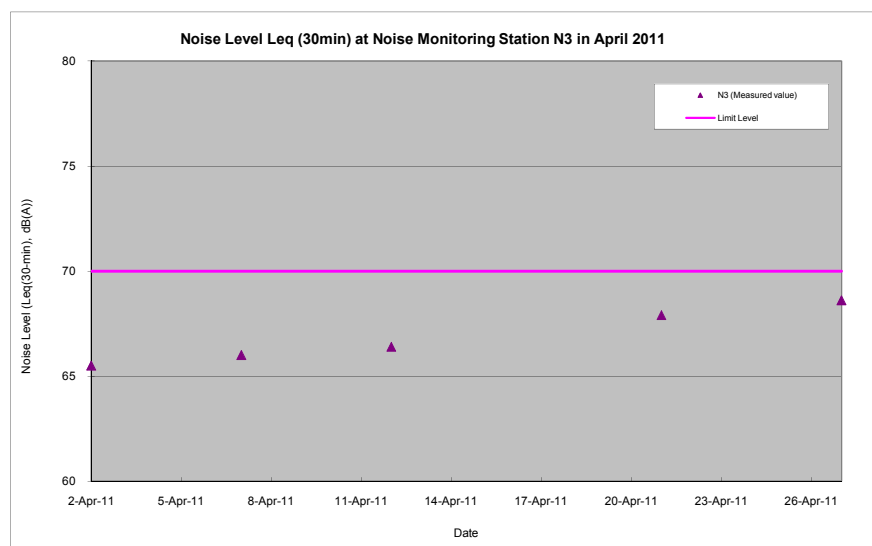


Note: For compliance comparison, please refer to above table and report.

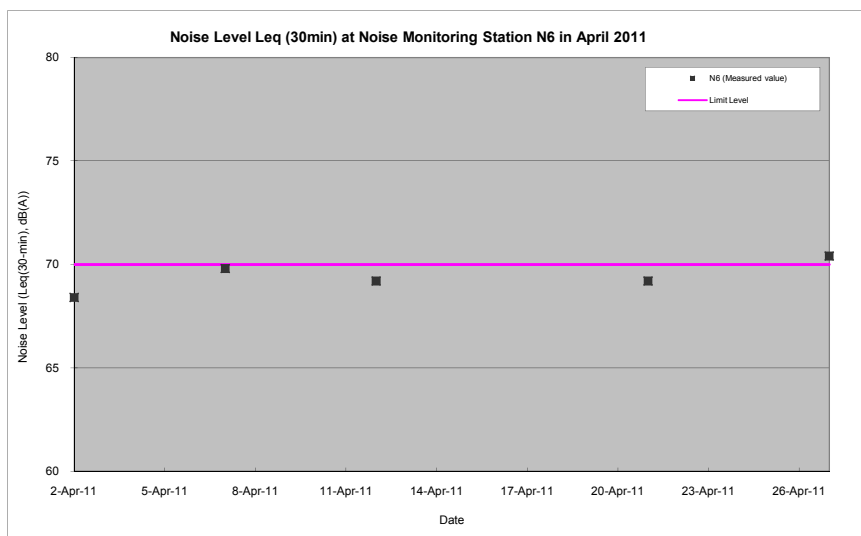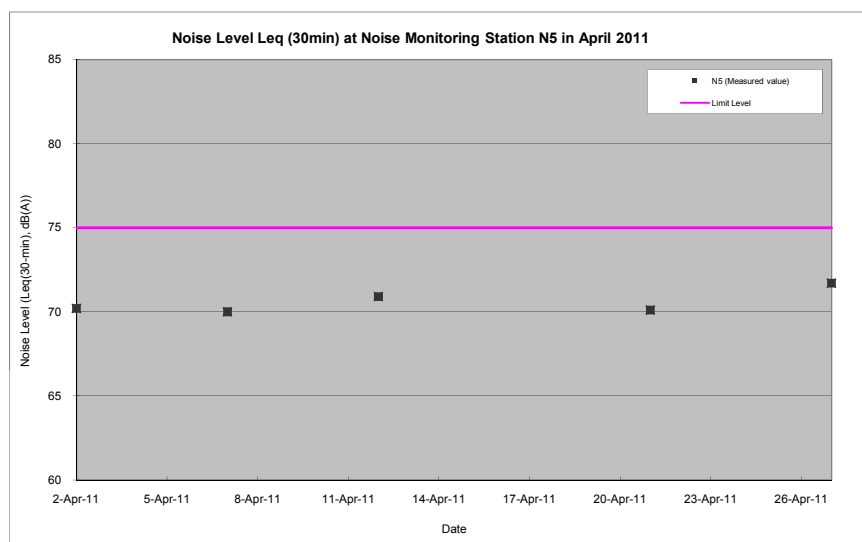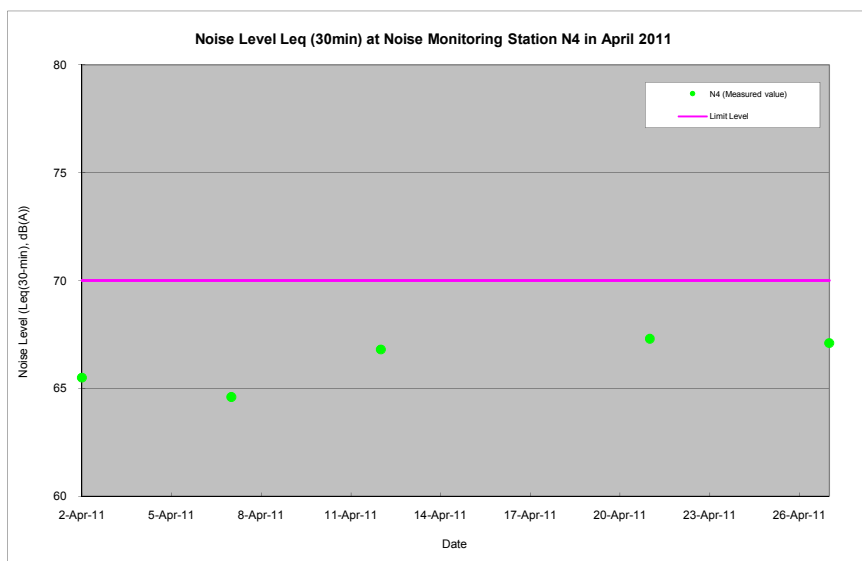


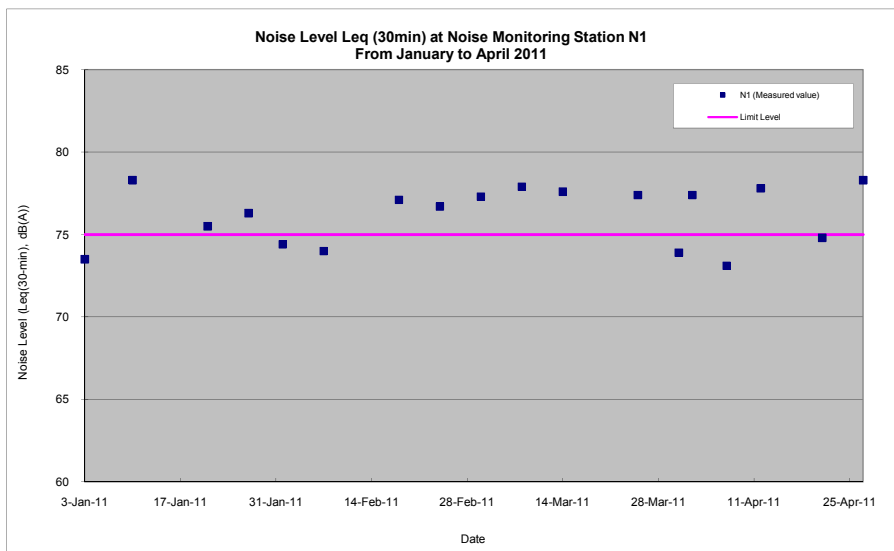


Note: For compliance comparison, please refer to above table and report.

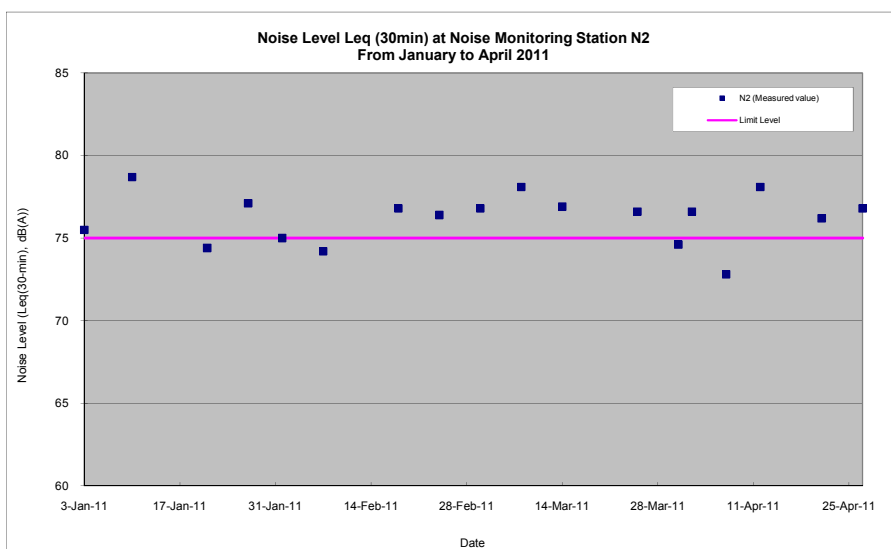


Note: For compliance comparison, please refer to above table and report.

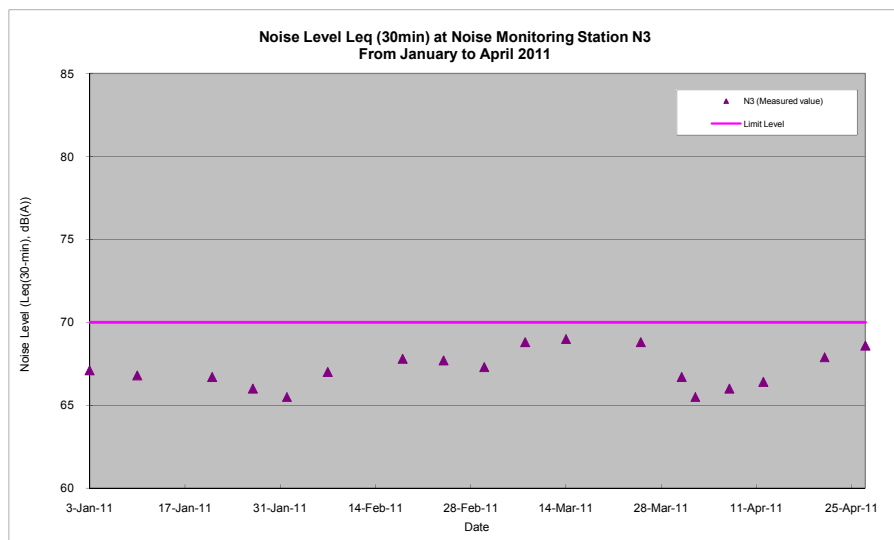


Note: For compliance comparison, please refer to above table and report.

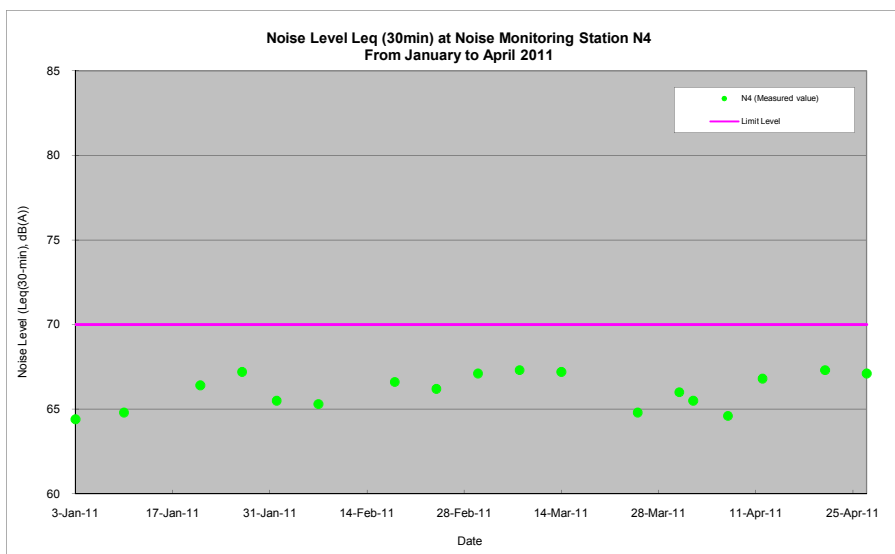

Note: For compliance comparison, please refer to above table and report.

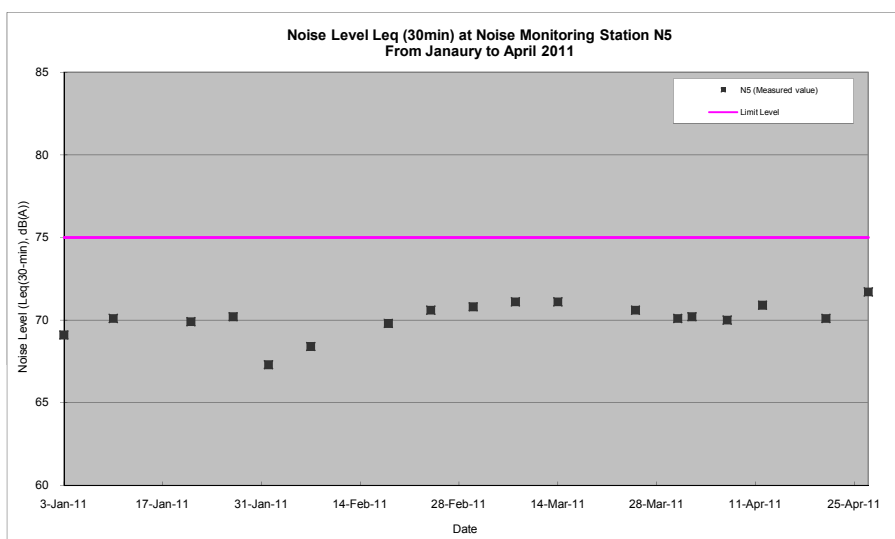

Note: For compliance comparison, please refer to above table and report.

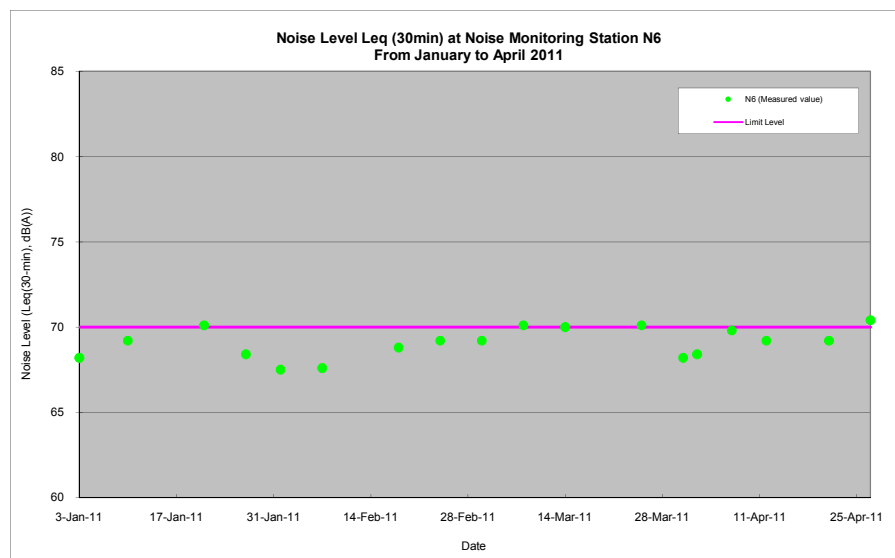

Note: For compliance comparison, please refer to above table and report.

Appendix I

**Landscape Summary
Report**

Design and Build of Traffic Improvements To Tuen Mun Road Town Centre Section

Total Tree No.	No of Contract	Numbers of Contract Tree + UTRA No.1
	Transplant	Transplant
	362	389
	Fell & Re.	Fell & Remove
	501	521
	1021	
	Retain	Retain
	134	102
	Missing	Missing
	0	9

Unnamed
Dead Tree (Removed)
In Progress
Completed
Total
Completed (%)

Fell & Remove Status	Crown Pruning	1st Root Pruning	2nd Root Pruning	3rd Root Pruning & Transplant
157				
9 (On Ting E.)				
43	37	46	71	84
478	352	343	318	305
521	389	389	389	389
92%	90%	88%	82%	78%

Item	Drawing No.	Tree No.	Chinese Name	Location	Rec., In Contract Document	Recommendation	Fell & Remove	Crown Pruning	1st Root Pruning	2nd Root Pruning	3rd Root Pruning & Transplant	Remarks
1	6106	TW0001	石栗	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	08-Apr-11	11-Apr-11	Not Yet	Not Yet	
2	6106	TW0002	石栗	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	08-Apr-11	11-Apr-11	Not Yet	Not Yet	
3	6106	TW0003	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	07-Apr-11	24-Dec-10	16-Feb-11	07-Apr-11	Transplanted
4	6106	TW0004	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	11-Apr-11	24-Dec-10	16-Feb-11	11-Apr-11	Transplanted
5	6106	TW0012	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
6	6106	TW0013	檸檬桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
7	6106	TW0014	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	08-Apr-11	-	-	-	-	
8	6106	TW0015	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
9	6106	TW0016	檸檬桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
10	6106	TW0021	白千層	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
11	6106	TW0022	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	11-Apr-11	29-Dec-10	17-Feb-11	11-Apr-11	Transplanted
12	6106	TW0023	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	08-Apr-11	-	-	-	-	
13	6106	TW0024	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	08-Apr-11	-	-	-	-	
14	6106	TW0025	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
15	6106	TW0026	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
16	6106	TW0030	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
17	6106	TW0033	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
18	6106	TW0034	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
19	6106	TW0035	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	08-Apr-11	-	-	-	-	
20	6106	TW0036	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
21	6106	TW0037	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
22	6106	TW0040	-	Tuen Mun Road near Kam Fai Garden	Retain	-	-	-	-	-	-	
23	6106	TW0043	白千層	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
24	6106	TW0044	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	13-Apr-11	31-Dec-10	17-Feb-11	13-Apr-11	Transplanted
25	6106	TW0045	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	12-Apr-11	31-Dec-10	18-Feb-11	12-Apr-11	Transplanted
26	6106	TW0046	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	12-Apr-11	12-Jan-11	18-Feb-11	12-Apr-11	Transplanted
27	6106	TW0047	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
28	6106	TW0049	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
29	6106	TW0050	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
30	6106	TW0054	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
31	6106	TW0055	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Apr-11	-	-	-	-	
32	6106	TW0056	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
33	6106	TW0057	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	

34	6106	TW0058	雙翼豆	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
35	6106	TW0061	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
36	6106	TW0062	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
37	6106	TW0066	檸檬桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
38	6106	TW0071	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
39	6106	TW0072	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
40	6106	TW0073	大葉桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
41	6106	TW0074	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	13-Apr-11	13-Jan-11	18-Feb-11	13-Apr-11	Transplanted
42	6106	TW0075	白千層	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	13-Apr-11	13-Jan-11	18-Feb-11	13-Apr-11	Transplanted
43	6106	TW0076	白千層	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
44	6106	TW0079	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
45	6106	TW0080	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
46	6106	TW0081	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
47	6106	TW0082	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
48	6106	TW0083	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
49	6106	TW0088	檸檬桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
50	6106	TW0089	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
51	6106	TW0090	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
52	6106	TW0093	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
53	6106	TW0095	大葉桉	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
54	6106	TW0096	死樹	Tuen Mun Road near Kam Fai Garden	Remove	Remove	-	-	-	-	-	
55	6106	TW0097	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
56	6106	TW0102	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
57	6106	TW0104	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
58	6106	TW0106	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
59	6106	TW0107	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
60	6106	TW0108	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Nov-10	-	-	-	-	
61	6106	TW0112	木麻黃	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
62	6106	TW0113	山指甲	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
63	6106	TW0114	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
64	6106	TW0115	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
65	6106	TW0116	台灣相思	Tuen Mun Road near Kam Fai Garden	Retain	Retain	-	-	-	-	-	
66	6106	TW0117	木麻黃	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
67	6106	TW0118	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
68	6106	TW0119	木麻黃	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
69	6106	TW0120	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
70	6106	TW0121	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
71	6106	TW0122	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
72	6106	TW0123	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
73	6106	TW0124	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
74	6106	TW0125	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
75	6106	TW0126	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
76	6106	TW0127	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
77	6106	TW0128	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
78	6106	TW0130	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
79	6106	TW0131	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
80	6106	TW0132	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
81	6106	TW0133	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
82	6106	TW0134	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
83	6106	TW0135	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	

84	6106	TW0136	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
85	6106	TW0137	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
86	6106	TW0138	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
87	6106	TW0139	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
88	6106	TW0140	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
89	6106	TW0141	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
90	6106	TW0142	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
91	6106	TW0143	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
92	6106	TW0144	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
93	6106	TW0145	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
94	6106	TW0146	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
95	6106	TW0147	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
96	6106	TW0148	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
97	6106	TW0149	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
98	6106	TW0150	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	10-Nov-10	-	-	-	-	
99	6106	TW0151	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
100	6106	TW0152	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
101	6106	TW0153	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
102	6106	TW0154	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
103	6106	TW0155	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
104	6106	TW0156	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
105	6106	TW0157	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
106	6106	TW0158	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
107	6106	TW0159	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
108	6106	TW0160	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
109	6106	TW0161	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	16-Aug-10	-	-	-	-	
110	6106	TW0162	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	16-Aug-10	-	-	-	-	
111	6106	TW0163	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	16-Aug-10	-	-	-	-	
112	6106	TW0165	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	18-Aug-10	-	-	-	-	
113	6106	TW0166	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
114	6106	TW0167	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
115	6106	TW0168	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
116	6106	TW0169	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
117	6106	TW0170	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
118	6106	TW0171	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
119	6106	TW0172	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
120	6106	TW0173	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
121	6106	TW0174	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
122	6106	TW0175	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
123	6106	TW0176	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Aug-10	-	-	-	-	
124	6106	TW0177	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Aug-10	-	-	-	-	
125	6106	TW0178	銀合歡	Tuen Mun Road near Kam Fai Garden	Remove	Remove	13-Aug-10	-	-	-	-	
126	6106	TW0179	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Aug-10	-	-	-	-	
127	6106	TW0180	垂葉榕	Tuen Mun Road near Kam Fai Garden	Transplant	Transplant	N/A	03-Apr-11	03-Apr-11	03-Apr-11	03-Apr-11	Transplanted
128	6106	TW0181	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
129	6106	TW0182	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
130	6106	TW0183	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
131	6106	TW0185	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
132	6106	TW0186	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Aug-10	-	-	-	-	
133	6106	TW0187	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	12-Aug-10	-	-	-	-	

134	6106	TW0188	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
135	6106	TW0189	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
136	6106	TW0190	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
137	6106	TW0191	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	13-Aug-10	-	-	-	-	
138	6106	TW0192	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
139	6106	TW0193	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
140	6106	TW0194	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
141	6106	TW0195	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
142	6106	TW0196	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	14-Aug-10	-	-	-	-	
143	6106	TW0197	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
144	6106	TW0198	檸檬桉	Tuen Mun Road near Kam Fai Garden	Fell	Fell	Not Yet	-	-	-	-	
145	6106	TW0199	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
146	6106	TW0200	台灣相思	Tuen Mun Road near Kam Fai Garden	Fell	Fell	11-Aug-10	-	-	-	-	
147	6105	TW0580	宮粉羊蹄甲	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	30-Oct-10	01-Nov-10	Transplanted
148	6105	TW0581	大葉合歡	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	06-Sep-10	24-Sep-10	Not Yet	Not Yet	
149	6105	TW0582	死樹	Wong Chu Road near Ting Fuk House	Remove	Remove	29-May-10	-	-	-	-	Ref. letter 115
150	6105	TW0583	菩提樹	Wong Chu Road near Ting Fuk House	Transplant	Retain	N/A	-	-	-	-	
151	6105	TW0584	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Retain	N/A	-	-	-	-	
152	6105	TW0585	菩提樹	Wong Chu Road near Ting Fuk House	Transplant	Retain	N/A	-	-	-	-	
153	6105	TW0586	宮粉羊蹄甲	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Sep-10	08-Sep-10	30-Oct-10	01-Nov-10	Transplanted
154	6105	TW0587	-	Wong Chu Road near Ting Fuk House	Transplant	Missing	20-Jan-11	-	-	-	-	Poor Health
155	6104	TW0588	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Transplant	20-Jan-11	-	-	-	-	Poor Health
156	6104	TW0589	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
157	6104	TW0590	朴樹	Wong Chu Road near Ting Fuk House	Fell	Fell	29-May-10	-	-	-	-	
158	6104	TW0591	石栗	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	10-Aug-10	24-Sep-10	30-Oct-10	Transplanted
159	6104	TW0592	石栗	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	19-Aug-10	22-Sep-10	30-Oct-10	Transplanted
160	6104	TW0593	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
161	6104	TW0594	木棉	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	19-Aug-10	22-Sep-10	11-Oct-10	Transplanted
162	6104	TW0595	石栗	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	19-Aug-10	22-Sep-10	29-Oct-10	Transplanted
163	6104	TW0596	木棉	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	10-Aug-10	22-Sep-10	11-Oct-10	Transplanted
164	6104	TW0597	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
165	6104	TW0598	-	Wong Chu Road near Ting Fuk House	Fell	-	29-May-10	-	-	-	-	
166	6104	TW0599	-	Wong Chu Road near Ting Fuk House	Fell	-	29-May-10	-	-	-	-	
167	6104	TW0600	木棉	Wong Chu Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	19-Aug-10	22-Sep-10	11-Oct-10	Transplanted
168	6104	TW0601	雙翼豆	Wong Chu Road near Ting Fuk House	Transplant	Transplant	20-Jan-11	-	-	-	-	Poor Health
169	6104	TW0603	石栗	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	05-Mar-11	06-Apr-11	Not Yet	
170	6104	TW0604	雙翼豆	Tuen Mun Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
171	6104	TW0605	石栗	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	07-Aug-10	05-Mar-11	06-Apr-11	Not Yet	
172	6104	TW0606	雙翼豆	Tuen Mun Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
173	6104	TW0607	雙翼豆	Tuen Mun Road near Ting Fuk House	Transplant	Fell	29-May-10	-	-	-	-	Ref. letter 115
174	6104	TW0608	細葉榕	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
175	6104	TW0609	細葉榕	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
176	6104	TW0610	細葉榕	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
177	6104	TW0611	細葉榕	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	22-Sep-10	22-Sep-10	02-Nov-10	Not Yet	
178	6104	TW0612	細葉榕	Tuen Mun Road near Ting Fuk House	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
179	6104	TW0613	銀合歡	Tuen Mun Road near Ting Fuk House	Remove	Remove	29-Aug-10	-	-	-	-	
180	6104	TW0614	細葉榕	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	10-Sep-10	Not Yet	Not Yet	Not Yet	
181	6104	TW0615	細葉榕	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	10-Sep-10	Not Yet	Not Yet	Not Yet	
182	6104	TW0616	阿江欖仁	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	10-Sep-10	28-Sep-10	16-Nov-10	18-Nov-10	Transplanted
183	6104	TW0617	鳳凰木	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	10-Sep-10	16-Sep-10	02-Nov-10	18-Nov-10	Transplanted

184	6104	TW0618	阿江欖仁	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	10-Sep-10	30-Sep-10	16-Nov-10	17-Nov-10	Transplanted
185	6104	TW0619	阿江欖仁	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	10-Sep-10	30-Sep-10	16-Nov-10	17-Nov-10	Transplanted
186	6104	TW0620	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
187	6104	TW0621	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	22-Aug-10	-	-	-	-	
188	6104	TW0622	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	22-Aug-10	-	-	-	-	
189	6104	TW0623	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
190	6104	TW0624	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
191	6104	TW0625	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
192	6104	TW0626	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
193	6104	TW0627	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
194	6104	TW0628	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-Aug-10	-	-	-	-	
195	6104	TW0629	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	22-Aug-10	-	-	-	-	
196	6104	TW0630	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	22-Aug-10	-	-	-	-	
197	6104	TW0631	黃葛樹	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	22-Aug-10	-	-	-	-	
198	6104	TW0632	-	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Missing	-	-	-	-	-	
199	6104	TW0633	雙翼豆	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	29-Sep-10	29-Sep-10	15-Nov-10	19-Nov-10	Transplanted
200	6104	TW0634	雙翼豆	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	18-Dec-10	28-Sep-10	29-Sep-10	15-Nov-10	-	Rootball size = 0.5m
201	6104	TW0635	石栗	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	05-Sep-10	-	-	-	-	
202	6104	TW0636	銀合歡	Tuen Mun Road near Luk Cheung Kwong College	Remove	Remove	05-Sep-10	-	-	-	-	
203	6104	TW0637	黃花夾竹桃	Tuen Mun Road near Luk Cheung Kwong College	Transplant	Transplant	N/A	17-Sep-10	17-Sep-10	02-Nov-10	09-Nov-10	Transplanted
204	6104	TW0638	黃花夾竹桃	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	05-Sep-10	-	-	-	-	
205	6104	TW0639	台灣相思	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	29-May-10	-	-	-	-	Ref. letter 115
206	6104	TW0640	石栗	Tuen Mun Road near Luk Cheung Kwong College	Fell	Fell	05-Sep-10	-	-	-	-	
207	6104	TW0641	-	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	-	-	-	-	-	-	
208	6104	TW0642	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
209	6104	TW0643	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
210	6104	TW0644	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
211	6104	TW0645	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
212	6104	TW0646	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
213	6104	TW0647	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Retain	Retain	-	-	-	-	-	
214	6104	TW0677	大葉合歡	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
215	6104	TW0678	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
216	6104	TW0679	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
217	6103	TW0680	-	Tuen Mun Road Slip Road to Tuen Hing Road	Remove	-	-	-	-	-	-	
218	6103	TW0681	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
219	6103	TW0682	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
220	6103	TW0683	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
221	6103	TW0684	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
222	6103	TW0685	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
223	6103	TW0686	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
224	6103	TW0687	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
225	6103	TW0688	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
226	6103	TW0689	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
227	6103	TW0690	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
228	6103	TW0691	-	Tuen Mun Road Slip Road to Tuen Hing Road	Missing	Retain	-	-	-	-	-	
229	6103	TW0692	-	Tuen Mun Road Slip Road to Tuen Hing Road	Remove	-	-	-	-	-	-	
230	6103	TW0693	台灣相思	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
231	6103	TW0694	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
232	6103	TW0695	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
233	6103	TW0696	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work

234	6103	TW0697	大葉合歡	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
235	6103	TW0698	宮粉羊蹄甲	Tuen Hi Road near Tuen Mun Road (YL/B)	Fell	Retain	13-Mar-11	-	-	-	-	Night Work
236	6103	TW0699	宮粉羊蹄甲	Tuen Hi Road near Tuen Mun Road (YL/B)	Retain	Retain	-	-	-	-	-	
237	6103	TW0700	黃葛樹	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
238	6103	TW0701	石栗	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
239	6103	TW0702	石栗	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
240	6103	TW0703	石栗	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
241	6103	TW0704	石栗	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
242	6103	TW0705	白千層	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
243	6103	TW0706	黃葛樹	Tuen Fat Road near Tuen Lee Street	Fell	Fell	12-Oct-10	-	-	-	-	Night Work
244	6102	TW0707	石栗	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
245	6102	TW0708	-	Tuen Fat Road near Tuen Yan Street	Fell	-	08-Oct-10	-	-	-	-	Night Work
246	6102	TW0709	石栗	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
247	6102	TW0710	黃葛樹	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
248	6102	TW0711	鳳凰木	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
249	6102	TW0712	白千層	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
250	6102	TW0713	白千層	Tuen Fat Road near Tuen Yan Street	Fell	Fell	09-Oct-10	-	-	-	-	Night Work
251	6102	TW0714	石栗	Tuen Fat Road near Tuen Yan Street	Fell	Fell	09-Oct-10	-	-	-	-	Night Work
252	6102	TW0715	石栗	Tuen Fat Road near Tuen Yan Street	Fell	Fell	08-Oct-10	-	-	-	-	Night Work
253	6102	TW0716	鳳凰木	Tuen Fat Road near Tuen Yan Street	Fell	Fell	09-Oct-10	-	-	-	-	Night Work
254	6102	TW0717	木棉	Tuen Fat Road near Tuen Yan Street	Fell	Fell	09-Oct-10	-	-	-	-	Night Work
255	6102	TW0718	石栗	Tuen Fat Road near Tuen Yan Street	Fell	Fell	09-Oct-10	-	-	-	-	Night Work
256	6101	TW0719	白千層	Centre Median near Yan Oi Tong	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
257	6101	TW0720	白千層	Centre Median near Yan Oi Tong	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
258	6101	TW0722	大葉桉	Centre Median near Yan Oi Tong	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
259	6102	TW0723	-	Centre Median near Tuen Yan Street	Fell	-	-	-	-	-	-	Missing
260	6102	TW0724	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
261	6102	TW0725	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
262	6102	TW0726	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
263	6102	TW0727	假欖榔	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
264	6102	TW0728	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
265	6102	TW0729	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
266	6102	TW0730	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
267	6102	TW0731	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
268	6102	TW0732	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
269	6102	TW0733	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
270	6102	TW0734	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
271	6102	TW0735	石栗	Centre Median near Tuen Yan Street	Fell	Fell	15-Oct-10	-	-	-	-	Night Work
272	6102	TW0736	木棉	Centre Median near Tuen Yan Street	Fell	Fell	15-Oct-10	-	-	-	-	Night Work
273	6102	TW0737	石栗	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
274	6102	TW0738	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
275	6102	TW0739	白千層	Centre Median near Tuen Yan Street	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
276	6102	TW0740	黃葛樹	Centre Median near Tuen Yan Street	Fell	Fell	15-Oct-10	-	-	-	-	Night Work
277	6102	TW0741	石栗	Centre Median near Tuen Yan Street	Fell	Fell	19-Oct-10	-	-	-	-	Night Work
278	6102	TW0742	石栗	Centre Median near Tuen Yan Street	Fell	Fell	14-Oct-10	-	-	-	-	Night Work
279	6102	TW0743	黃葛樹	Centre Median near Tuen Yan Street	Fell	Fell	19-Oct-10	-	-	-	-	Night Work
280	6102	TW0744	石栗	Centre Median near Tuen Yan Street	Fell	Fell	19-Oct-10	-	-	-	-	Night Work
281	6102	TW0745	石栗	Centre Median near Tuen Yan Street	Fell	Fell	14-Oct-10	-	-	-	-	Night Work
282	6102	TW0746	石栗	Centre Median between Tuen Shing St & Tuen Hing Rd	Fell	Fell	13-Oct-10	-	-	-	-	Night Work
283	6102	TW0747	白千層	Centre Median between Tuen Shing St & Tuen Hing Rd	Fell	Fell	13-Oct-10	-	-	-	-	Night Work

[illegible]

334	6103	TW0798	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
335	6103	TW0799	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	10-Nov-10	-	-	-	-	Night Work
336	6103	TW0800	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
337	6103	TW0801	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	10-Nov-10	-	-	-	-	Night Work
338	6103	TW0802	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	10-Nov-10	-	-	-	-	Night Work
339	6103	TW0803	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	10-Nov-10	-	-	-	-	Night Work
340	6103	TW0804	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	10-Nov-10	-	-	-	-	Night Work
341	6103	TW0805	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	10-Nov-10	-	-	-	-	Night Work
342	6104	TW0806	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	10-Nov-10	-	-	-	-	Night Work
343	6104	TW0807	木麻黃	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
344	6104	TW0808	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
345	6104	TW0809	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	04-Nov-10	-	-	-	-	Night Work
346	6104	TW0810	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	04-Nov-10	-	-	-	-	Night Work
347	6104	TW0811	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	04-Nov-10	-	-	-	-	Night Work
348	6104	TW0812	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	04-Nov-10	-	-	-	-	Night Work
349	6104	TW0813	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
350	6104	TW0814	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
351	6104	TW0815	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	09-Nov-10	-	-	-	-	Night Work
352	6104	TW0816	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	03-Nov-10	-	-	-	-	Night Work
353	6104	TW0817	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	04-Nov-10	-	-	-	-	Night Work
354	6104	TW0818	石栗	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	03-Nov-10	-	-	-	-	Night Work
355	6104	TW0819	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	03-Nov-10	-	-	-	-	Night Work
356	6104	TW0820	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	03-Nov-10	-	-	-	-	
357	6104	TW0821	黃葛樹	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	03-Nov-10	-	-	-	-	Night Work
358	6104	TW0822	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
359	6104	TW0823	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
360	6104	TW0824	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
361	6104	TW0825	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
362	6104	TW0826	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
363	6104	TW0827	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
364	6104	TW0828	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
365	6104	TW0829	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
366	6104	TW0830	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
367	6104	TW0831	白千層	Centre Median between Tuen Hing Rd & Chi Lok Fa Yue	Fell	Fell	02-Nov-10	-	-	-	-	Night Work
368	6103	TW0832	大葉合歡	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
369	6103	TW0833	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
370	6103	TW0834	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
371	6103	TW0835	大葉合歡	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
372	6103	TW0836	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
373	6103	TW0837	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Remove	07-Sep-10	-	-	-	-	by other
374	6103	TW0838	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	-	-	-	-	-	Missing
375	6103	TW0839	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	Night Work
376	6103	TW0840	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	-	-	-	-	-	Missing
377	6103	TW0841	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Remove	07-Sep-10	-	-	-	-	by other
378	6103	TW0842	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Remove	07-Sep-10	-	-	-	-	by other
379	6103	TW0843	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	07-Sep-10	-	-	-	-	by other
380	6103	TW0844	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Remove	07-Sep-10	-	-	-	-	by other
381	6103	TW0845	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	-	-	-	-	-	Missing
382	6103	TW0846	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	07-Sep-10	-	-	-	-	by other
383	6103	TW0847	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	

384	6103	TW0848	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	23-Nov-10	-	-	-	-	Night Work
385	6103	TW0849	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	23-Nov-10	-	-	-	-	Night Work
386	6103	TW0851	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	23-Nov-10	-	-	-	-	Night Work
387	6103	TW0852	台灣相思	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	16-Sep-10	-	-	-	-	
388	6103	TW0853	-	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	-	-	-	-	-	-	Missing
389	6103	TW0854	桑	Tuen Hing Road Slip Road to Tuen Mun Road B bound	Fell	Fell	23-Nov-10	-	-	-	-	Night Work
390	6103	TW0855	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	21-Oct-10	-	-	-	-	Night Work
391	6103	TW0856	-	Tuen Hi Road near Tuen Wui Street	Fell	-	-	-	-	-	-	Missing
392	6103	TW0857	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	30-Oct-10	-	-	-	-	Night Work
393	6103	TW0858	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	21-Oct-10	-	-	-	-	Night Work
394	6103	TW0859	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	30-Oct-10	-	-	-	-	Night Work
395	6103	TW0860	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	21-Oct-10	-	-	-	-	Night Work
396	6103	TW0861	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	30-Oct-10	-	-	-	-	Night Work
397	6103	TW0862	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	30-Oct-10	-	-	-	-	Night Work
398	6103	TW0863	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	30-Oct-10	-	-	-	-	Night Work
399	6103	TW0864	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	28-Oct-10	-	-	-	-	Night Work
400	6103	TW0865	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	26-Oct-10	-	-	-	-	Night Work
401	6103	TW0866	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
402	6103	TW0867	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
403	6103	TW0868	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
404	6103	TW0869	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
405	6103	TW0870	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	26-Oct-10	-	-	-	-	Night Work
406	6103	TW0871	-	Tuen Hi Road near Tuen Wui Street	Fell	-	-	-	-	-	-	Missing
407	6103	TW0872	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	26-Oct-10	-	-	-	-	Night Work
408	6103	TW0873	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	26-Oct-10	-	-	-	-	Night Work
409	6103	TW0874	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	28-Oct-10	-	-	-	-	Night Work
410	6103	TW0875	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	28-Oct-10	-	-	-	-	Night Work
411	6103	TW0876	木棉	Tuen Hi Road near Tuen Wui Street	Fell	Fell	21-Oct-10	-	-	-	-	Night Work
412	6103	TW0877	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
413	6103	TW0878	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	29-Oct-10	-	-	-	-	Night Work
414	6103	TW0879	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	28-Oct-10	-	-	-	-	Night Work
415	6103	TW0880	黃葛樹	Tuen Hi Road near Tuen Wui Street	Fell	Fell	28-Oct-10	-	-	-	-	Night Work
416	6102	TW0881	秋楓	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	31-Aug-10	07-Oct-10	17-Dec-10	17-Mar-11	Transplanted
417	6102	TW0882	秋楓	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	31-Aug-10	06-Sep-10	07-Oct-10	12-Mar-11	Transplanted
418	6102	TW0883	秋楓	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	31-Aug-10	04-Sep-10	07-Oct-10	12-Mar-11	Transplanted
419	6102	TW0884	苦楝	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	27-Sep-10	28-Sep-10	23-Mar-11	24-Mar-11	31/8 First Time
420	6102	TW0885	苦楝	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	27-Sep-10	28-Sep-10	23-Mar-11	24-Mar-11	31/8 First Time
421	6102	TW0886	秋楓樹	Tuen Mun Road A Bound near Tuen Lung Street	Transplant	Transplant	N/A	27-Sep-10	07-Oct-10	28-Mar-11	29-Mar-11	31/8 First Time
422	6102	TW0887	白千層	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	12-Nov-10	-	-	-	-	
423	6102	TW0888	白千層	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	25-Sep-10	25-Sep-10	09-Nov-10	17-Jan-11	Transplanted
424	6102	TW0889	白千層	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	12-Nov-10	-	-	-	-	
425	6101	TW0890	白千層	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	12-Nov-10	-	-	-	-	
426	6101	TW0891	樹頭菜	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	30-Aug-10	06-Oct-10	09-Nov-10	Transplanted
427	6101	TW0892	樹頭菜	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	01-Sep-10	06-Oct-10	08-Nov-10	Transplanted
428	6101	TW0893	樹頭菜	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	31-Aug-10	06-Oct-10	08-Nov-10	Transplanted
429	6101	TW0894	樹頭菜	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	31-Aug-10	06-Oct-10	08-Nov-10	Transplanted
430	6101	TW0895	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	02-Sep-10	20-Nov-10	20-Nov-10	Transplanted
431	6101	TW0896	洋紫荊	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	04-Sep-10	06-Oct-10	04-Nov-10	Transplanted
432	6101	TW0897	洋紫荊	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	30-Aug-10	05-Oct-10	04-Nov-10	Transplanted
433	6101	TW0898	洋紫荊	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	04-Sep-10	05-Oct-10	04-Nov-10	Transplanted

434	6101	TW0899	洋紫荆	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	03-Sep-10	05-Oct-10	08-Nov-10	Transplanted
435	6101	TW0900	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	04-Sep-10	05-Oct-10	06-Dec-10	Transplanted
436	6101	TW0901	樹頭菜	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	05-Oct-10	08-Nov-10	Transplanted
437	6101	TW0902	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	09-Oct-10	09-Apr-11	09-Apr-11	Undergr'd UU
438	6101	TW0903	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	04-Oct-10	07-Dec-10	Transplanted
439	6101	TW0904	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	04-Oct-10	09-Nov-10	Transplanted
440	6101	TW0905	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	04-Sep-10	05-Oct-10	20-Nov-10	Transplanted
441	6101	TW0906	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	03-Sep-10	04-Oct-10	06-Dec-10	Transplanted
442	6101	TW0907	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	20-Aug-10	03-Sep-10	04-Oct-10	07-Dec-10	Transplanted
443	6101	TW0908	洋紫荆	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	04-Sep-10	07-Oct-10	11-Dec-10	Transplanted
444	6101	TW0909	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	04-Sep-10	09-Dec-10	09-Dec-10	Transplanted
445	6101	TW0910	石栗	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	04-Sep-10	09-Dec-10	09-Dec-10	Transplanted
446	6101	TW0911	烏柏	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	03-Sep-10	08-Dec-10	08-Dec-10	Transplanted
447	6101	TW0912	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	10-Dec-10	10-Dec-10	10-Dec-10	Transplanted
448	6101	TW0913	烏柏	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	04-Sep-10	13-Dec-10	13-Dec-10	Transplanted
449	6101	TW0914	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	03-Sep-10	06-Oct-10	15-Dec-10	Transplanted
450	6101	TW0915	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	02-Sep-10	06-Oct-10	15-Dec-10	Transplanted
451	6101	TW0916	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	15-Dec-10	30-Aug-10	02-Sep-10	06-Oct-10	-	Poor Health
452	6101	TW0917	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	01-Sep-10	02-Sep-10	15-Dec-10	18-Jan-11	Transplanted
453	6101	TW0918	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
454	6101	TW0919	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	02-Sep-10	04-Oct-10	15-Dec-10	Transplanted
455	6101	TW0920	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	by other
456	6101	TW0921	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
457	6101	TW0922	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	04-Oct-10	15-Dec-10	Transplanted
458	6101	TW0923	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
459	6101	TW0924	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
460	6101	TW0925	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
461	6101	TW0926	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
462	6101	TW0927	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
463	6101	TW0928	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
464	6101	TW0929	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
465	6101	TW0930	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
466	6101	TW0931	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
467	6101	TW0932	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	04-Oct-10	04-Jan-11	Night Work
468	6101	TW0933	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	04-Oct-10	04-Jan-11	Night Work
469	6101	TW0934	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	05-Oct-10	04-Jan-11	Night Work
470	6101	TW0935	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
471	6101	TW0936	石栗	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
472	6101	TW0937	大葉桉	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
473	6101	TW0938	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	05-Oct-10	05-Jan-11	Night Work
474	6101	TW0939	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	30-Aug-10	03-Sep-10	05-Oct-10	05-Jan-11	Night Work
475	6101	TW0940	石栗	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
476	6101	TW0941	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	31-Dec-10	-	-	-	-	Night Work
477	6101	TW0942	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
478	6101	TW0943	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	05-Oct-10	04-Jan-11	Night Work
479	6101	TW0944	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
480	6101	TW0945	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	05-Oct-10	05-Jan-11	Night Work
481	6101	TW0946	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	27-Oct-10	-	-	-	-	Night Work
482	6101	TW0947	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Transplant	Transplant	N/A	07-Sep-10	07-Sep-10	05-Oct-10	05-Jan-11	Night Work
483	6101	TW0948	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	10-Sep-10	-	-	-	-	Night Work

484	6101	TW0949	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	10-Sep-10	-	-	-	-	Night Work
485	6101	TW0950	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	08-Sep-10	-	-	-	-	Night Work
486	6101	TW0951	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	10-Sep-10	-	-	-	-	Night Work
487	6101	TW0952	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	08-Sep-10	-	-	-	-	Night Work
488	6101	TW0953	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	08-Sep-10	-	-	-	-	Night Work
489	6101	TW0954	串錢柳	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	08-Sep-10	-	-	-	-	Night Work
490	6101	TW0955	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Fell	Fell	08-Sep-10	-	-	-	-	Night Work
491	6101	TW0956	-	Tuen Mun Road A Bound near Yan Ching Street	Remove	-	-	-	-	-	-	Missing
492	6101	TW0957	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
493	6101	TW0959	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
494	6101	TW0960	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
495	6101	TW0961	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
496	6101	TW0962	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
497	6101	TW0963	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
498	6101	TW0966	鳳凰木	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
499	6101	TW0969	假檳榔	Tuen Mun Road A Bound near Yan Ching Street	Retain	Retain	-	-	-	-	-	
500	6101	TW0973	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	18-Dec-10	Not Yet	
501	6101	TW0974	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	18-Dec-10	Not Yet	
502	6101	TW0975	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	17-Dec-10	Not Yet	
503	6101	TW0976	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	17-Dec-10	Not Yet	
504	6101	TW0977	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	18-Dec-10	Not Yet	
505	6101	TW0978	假檳榔	Yan Oi Tong Circuit Car Park	Transplant	Transplant	N/A	06-Nov-10	06-Nov-10	18-Dec-10	Not Yet	
506	6101	TW0979	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
507	6101	TW0980	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
508	6101	TW0981		Yan Oi Tong Circuit Planter Area	Remove	-	-	-	-	-	-	Missing
509	6101	TW0982	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	18-Nov-10	22-Nov-10	22-Nov-10	22-Nov-10	Transplanted
510	6101	TW0983	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	24-Nov-10	24-Nov-10	24-Nov-10	Transplanted
511	6101	TW0984	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	18-Nov-10	22-Nov-10	22-Nov-10	22-Nov-10	Transplanted
512	6101	TW0985	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Aug-10	10-Aug-10	10-Sep-10	15-Oct-10	Transplanted
513	6101	TW0986	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Aug-10	10-Aug-10	10-Sep-10	15-Oct-10	Transplanted
514	6101	TW0987	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Aug-10	10-Aug-10	10-Sep-10	15-Oct-10	Transplanted
515	6101	TW0988	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Aug-10	10-Aug-10	09-Sep-10	15-Oct-10	Transplanted
516	6101	TW0989	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Aug-10	10-Aug-10	09-Sep-10	27-Oct-10	Transplanted
517	6101	TW0990	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
518	6101	TW0991	大葉合歡	Yan Oi Tong Circuit Planter Area	Fell	Fell	14-Oct-10	-	-	-	-	
519	6101	TW0992	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
520	6101	TW0993	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
521	6101	TW0994	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Sep-10	17-Sep-10	14-Oct-10	14-Oct-10	Transplanted
522	6101	TW0995	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	24-Nov-10	24-Nov-10	24-Nov-10	Transplanted
523	6101	TW0996	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Sep-10	17-Sep-10	14-Oct-10	14-Oct-10	Transplanted
524	6101	TW0997	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	23-Nov-10	23-Nov-10	23-Nov-10	Transplanted
525	6101	TW0998	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	23-Nov-10	23-Nov-10	23-Nov-10	Transplanted
526	6101	TW0999	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
527	6101	TW1000	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
528	6101	TW1001	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	13-Oct-10	Transplanted
529	6101	TW1002	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	14-Oct-10	Transplanted
530	6101	TW1003	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	13-Oct-10	Transplanted
531	6101	TW1004	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	06-Aug-10	07-Sep-10	13-Oct-10	Transplanted
532	6101	TW1005	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	06-Aug-10	08-Sep-10	13-Oct-10	Transplanted
533	6101	TW1006	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	08-Sep-10	12-Oct-10	Transplanted

534	6101	TW1007	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	30-Aug-10	12-Oct-10	12-Oct-10	Transplanted
535	6101	TW1008	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	30-Aug-10	30-Aug-10	13-Oct-10	13-Oct-10	Transplanted
536	6101	TW1009	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	08-Sep-10	12-Oct-10	Transplanted
537	6101	TW1010	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	18-Nov-10	23-Nov-10	23-Nov-10	23-Nov-10	Transplanted
538	6101	TW1011	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	13-Oct-10	13-Oct-10	13-Oct-10	Transplanted
539	6101	TW1012	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	22-Nov-10	22-Nov-10	22-Nov-10	Transplanted
540	6101	TW1013	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	09-Aug-10	12-Oct-10	12-Oct-10	Transplanted
541	6101	TW1014	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	20-Aug-10	12-Oct-10	12-Oct-10	Transplanted
542	6101	TW1015	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	08-Sep-10	12-Oct-10	Transplanted
543	6101	TW1016	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	06-Aug-10	08-Sep-10	27-Oct-10	Transplanted
544	6101	TW1017	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	08-Sep-10	08-Oct-10	Transplanted
545	6101	TW1018	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	30-Aug-10	05-Oct-10	08-Oct-10	Transplanted
546	6101	TW1019	大葉合歡	Yan Oi Tong Circuit Planter Area	Fell	Fell	03-Aug-10	-	-	-	-	
547	6101	TW1020	大葉合歡	Yan Oi Tong Circuit Planter Area	Fell	Fell	02-Aug-10	-	-	-	-	
548	6101	TW1021	烏柏	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	07-Aug-10	08-Sep-10	08-Oct-10	Transplanted
549	6101	TW1022	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	25-Nov-10	25-Nov-10	25-Nov-10	Transplanted
550	6101	TW1023	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	07-Aug-10	10-Sep-10	08-Oct-10	Transplanted
551	6101	TW1024	烏柏	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	08-Oct-10	Transplanted
552	6101	TW1025	烏柏	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	Not Yet	Not Yet	Not Yet	
553	6101	TW1026	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	Not Yet	Not Yet	Not Yet	
554	6101	TW1027	大葉合歡	Yan Oi Tong Circuit Planter Area	Fell	Fell	03-Aug-10	-	-	-	-	
555	6101	TW1028	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	25-Nov-10	25-Nov-10	25-Nov-10	Transplanted
556	6101	TW1029	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	26-Nov-10	26-Nov-10	26-Nov-10	Transplanted
557	6101	TW1030	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	04-Apr-11	Not Yet	Not Yet	
558	6101	TW1031	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	04-Apr-11	Not Yet	Not Yet	
559	6101	TW1032	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	04-Apr-11	Not Yet	Not Yet	
560	6101	TW1033	大葉合歡	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
561	6101	TW1034	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	04-Apr-11	Not Yet	Not Yet	
562	6101	TW1035	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	01-Apr-11	Not Yet	Not Yet	
563	6101	TW1036	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	09-Sep-10	18-Oct-10	Transplanted
564	6101	TW1037	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	13-Nov-10	Transplanted
565	6101	TW1038	洋紫荊	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	09-Aug-10	09-Sep-10	19-Oct-10	Transplanted
566	6101	TW1039	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	18-Oct-10	Transplanted
567	6101	TW1040	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	18-Oct-10	Transplanted
568	6101	TW1041	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	18-Oct-10	Transplanted
569	6101	TW1042	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	18-Oct-10	Transplanted
570	6101	TW1043	串錢柳	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	03-Aug-10	09-Aug-10	09-Sep-10	18-Oct-10	Transplanted
571	6101	TW1044	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	01-Apr-11	Not Yet	Not Yet	
572	6101	TW1045	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	07-Aug-10	09-Sep-10	28-Oct-10	Transplanted
573	6101	TW1046	洋紫荊	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	04-Aug-10	09-Sep-10	13-Nov-10	13-Nov-10	Transplanted
574	6101	TW1047	鳳凰木	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	17-Nov-10	26-Nov-10	26-Nov-10	26-Nov-10	Transplanted
575	6101	TW1048	鳳凰木	Yan Oi Tong Circuit Planter Area	Fell	Retain	30-Mar-11	-	-	-	-	
576	6101	TW1049	洋紫荊	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	09-Sep-10	09-Sep-10	19-Oct-10	19-Oct-10	Transplanted
577	6101	TW1050	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	09-Sep-10	19-Oct-10	Transplanted
578	6101	TW1051	石栗	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	02-Apr-11	Not Yet	Not Yet	
579	6101	TW1052	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Transplant	N/A	02-Aug-10	07-Aug-10	09-Sep-10	19-Oct-10	Transplanted
580	6101	TW1053	大葉桉	Yan Oi Tong Circuit Planter Area	Fell	Fell	05-Aug-10	-	-	-	-	
581	6101	TW1054	假檳榔	Yan Oi Tong Circuit Planter Area	Transplant	Retain	N/A	30-Mar-11	01-Apr-11	Not Yet	Not Yet	
582	6101	TW1055	藍花楸	Yan Oi Tong Circuit Planter Area	Fell	Retain	30-Mar-11	-	-	-	-	
583	6101	TW1056	大葉桉	Yan Oi Tong Circuit Planter Area	Fell	Fell	05-Aug-10	-	-	-	-	

584	6101	TW1057	大葉桉	Yan Oi Tong Circuit Planter Area	Fell	Fell	05-Aug-10	-	-	-	-	
585	6101	TW1058	大葉桉	Yan Oi Tong Circuit Planter Area	Fell	Fell	04-Aug-10	-	-	-	-	
586	6101	TW1059	大葉桉	Yan Oi Tong Circuit Planter Area	Fell	Fell	04-Aug-10	-	-	-	-	
587	6101	TW1060	大葉合歡	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
588	6101	TW1061	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
589	6101	TW1062	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
590	6101	TW1063	-	Yan Oi Tong Circuit Planter Area	Remove	-	-	-	-	-	-	
591	6101	TW1065	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
592	6101	TW1066	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
593	6101	TW1067	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
594	6101	TW1068	石栗	Yan Oi Tong Circuit Planter Area	Retain	Retain	-	-	-	-	-	
595	6101	TW1069	鳳凰木	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
596	6101	TW1070	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	-	-	-	-	-	-	
597	6101	TW1071	大葉合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
598	6101	TW1072	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
599	6101	TW1073	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	-	-	-	-	-	-	
600	6101	TW1074	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
601	6101	TW1075	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
602	6101	TW1076	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
603	6101	TW1077	雙翼豆	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	15-Sep-10	-	-	-	-	Night Work
604	6101	TW1078	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
605	6101	TW1079	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
606	6101	TW1080	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
607	6101	TW1081	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
608	6101	TW1082	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
609	6101	TW1083	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
610	6101	TW1084	洋紫荊	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
611	6101	TW1085	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	-	-	-	-	-	-	
612	6101	TW1086	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
613	6101	TW1087	洋紫荊	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
614	6101	TW1088	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	
615	6101	TW1089	大葉合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
616	6101	TW1090	大葉合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
617	6101	TW1091	銀合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
618	6101	TW1092	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
619	6101	TW1093	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
620	6101	TW1094	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	27-Sep-10	-	-	-	-	
621	6101	TW1095	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
622	6101	TW1096	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Missing	-	-	-	-	-	Missing
623	6101	TW1097	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
624	6101	TW1098	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
625	6101	TW1099	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	29-Sep-10	-	-	-	-	
626	6109	TW1100	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
627	6109	TW1101	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
628	6109	TW1102	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
629	6109	TW1103	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
630	6109	TW1104	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
631	6109	TW1105	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
632	6109	TW1106	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
633	6109	TW1107	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	

634	6109	TW1108	銀合歡	Castle Peak Road near Site Office	Remove	Remove	01-Jun-10	-	-	-	-	
635	6105	TW1143	雙翼豆	Tsing Sin Playground	Transplant	Transplant	N/A	25-Aug-10	27-Aug-10	04-Oct-10	26-Oct-10	Transplanted
636	6105	TW1144	-	Tsing Sin Playground	Transplant	Missing	-	-	-	-	-	
637	6105	TW1145	雙翼豆	Tsing Sin Playground	Transplant	Transplant	N/A	25-Aug-10	27-Aug-10	04-Oct-10	26-Oct-10	Transplanted
638	6105	TW1146	雙翼豆	Tsing Sin Playground	Transplant	Transplant	N/A	25-Aug-10	27-Aug-10	04-Oct-10	26-Oct-10	Transplanted
639	6105	TW1147	-	Tsing Sin Playground	Transplant	Missing	-	-	-	-	-	
640	6105	TW1148	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	20-Sep-10	25-Oct-10	Transplanted
641	6105	TW1149	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	20-Sep-10	25-Oct-10	Transplanted
642	6105	TW1150	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	18-Sep-10	20-Oct-10	Transplanted
643	6105	TW1151	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	18-Sep-10	20-Oct-10	Transplanted
644	6105	TW1152	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	18-Sep-10	20-Oct-10	Transplanted
645	6105	TW1153	大花紫薇	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	18-Sep-10	20-Oct-10	Transplanted
646	6105	TW1154	細葉榕	Tsing Sin Playground	Transplant	Retain	-	-	-	-	-	-
647	6105	TW1155	細葉榕	Tsing Sin Playground	Transplant	Retain	-	-	-	-	-	-
648	6105	TW1156	細葉榕	Tsing Sin Playground	Transplant	Retain	-	-	-	-	-	-
649	6105	TW1157	細葉榕	Tsing Sin Playground	Transplant	Retain	-	-	-	-	-	-
650	6105	TW1158	馬拉巴栗	Tsing Hoi Circuit near RCP	Transplant	Transplant	N/A	31-Aug-10	02-Sep-10	04-Oct-10	25-Oct-10	Transplanted
651	6105	TW1161	血桐	Tsing Hoi Circuit near RCP	Fell	Fell	21-Aug-10	-	-	-	-	
652	6105	TW1162	黃花夾竹桃	Tsing Hoi Circuit near RCP	Fell	Fell	21-Aug-10	-	-	-	-	
653	6105	TW1163	黃花夾竹桃	Tsing Hoi Circuit near RCP	Fell	Fell	21-Aug-10	-	-	-	-	
654	6105	TW1164	黃花夾竹桃	Tsing Hoi Circuit near RCP	Fell	Fell	21-Aug-10	-	-	-	-	
655	6105	TW1165	銀合歡	Tsing Hoi Circuit near RCP	Remove	Remove	21-Aug-10	-	-	-	-	
656	6108	TW1166	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
657	6108	TW1167	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
658	6108	TW1168	白千層	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
659	6108	TW1169	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
660	6108	TW1170	白千層	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
661	6108	TW1171	串錢柳	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
662	6108	TW1172	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	Not Yet	Not Yet	Not Yet	
663	6108	TW1173	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	Not Yet	Not Yet	Not Yet	
664	6108	TW1174	木麻黃	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
665	6108	TW1182	木麻黃	Castle Peak Road J/O Fu Fat Lane	Retain	Retain	-	-	-	-	-	
666	6108	TW1183	南洋杉	Castle Peak Road J/O Fu Fat Lane	Retain	Retain	-	-	-	-	-	
667	6108	TW1185	南洋杉	Castle Peak Road J/O Fu Fat Lane	Retain	Retain	-	-	-	-	-	
668	6108	TW1186	南洋杉	Castle Peak Road J/O Fu Fat Lane	Retain	Retain	-	-	-	-	-	
669	6108	TW1187	木麻黃	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
670	6108	TW1190	串錢柳	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
671	6108	TW1191	串錢柳	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
672	6108	TW1192	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
673	6108	TW1193	串錢柳	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
674	6108	TW1194	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
675	6108	TW1195	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
676	6108	TW1196	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
677	6104	TW1200	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
678	6104	TW1201	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	05-Nov-10	-	-	-	-	
679	6104	TW1202	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	05-Nov-10	-	-	-	-	
680	6104	TW1203	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	05-Nov-10	-	-	-	-	
681	6104	TW1204	-	Tsing Hoi Circuit near Tsing Wu Square	Fell	-	-	-	-	-	-	Missing
682	6104	TW1205	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
683	6104	TW1206	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work

684	6104	TW1207	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
685	6104	TW1208	楓香	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
686	6104	TW1209	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
687	6104	TW1210	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
688	6104	TW1211	鳳凰木	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
689	6104	TW1212	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
690	6104	TW1213	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
691	6104	TW1214	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
692	6104	TW1215	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	13-Nov-10	-	-	-	-	Night Work
693	6104	TW1216	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
694	6104	TW1217	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
695	6104	TW1218	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
696	6104	TW1219	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
697	6104	TW1220	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
698	6104	TW1221	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
699	6104	TW1222	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
700	6104	TW1223	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
701	6104	TW1224	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
702	6104	TW1225	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
703	6104	TW1226	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
704	6104	TW1227	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
705	6104	TW1228	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
706	6104	TW1229	宮粉羊蹄甲	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
707	6104	TW1230	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
708	6104	TW1231	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	05-Nov-10	-	-	-	-	
709	6104	TW1232	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
710	6104	TW1233	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
711	6104	TW1234	黃槿	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	21-Oct-10	-	-	-	-	
712	6104	TW1235	木棉	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
713	6104	TW1236	石栗	Tsing Hoi Circuit near Tsing Wu Square	Fell	Fell	11-Nov-10	-	-	-	-	Night Work
714	6104	TW1237	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	14-Feb-11	22-Feb-11	Night Work
715	6104	TW1238	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	10-Aug-10	-	-	-	-	
716	6104	TW1239	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	15-Feb-11	26-Feb-11	Transplanted
717	6104	TW1240	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	14-Feb-11	24-Feb-11	Transplanted
718	6104	TW1241	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	15-Jan-11	08-Mar-11	Transplanted
719	6104	TW1242	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	15-Jan-11	08-Mar-11	Transplanted
720	6104	TW1243	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Transplant	Transplant	N/A	09-Aug-10	15-Dec-10	14-Jan-11	09-Mar-11	Transplanted
721	6104	TW1244	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
722	6103	TW1245	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
723	6103	TW1248	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
724	6103	TW1249	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
725	6103	TW1250	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
726	6103	TW1251	石栗	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
727	6103	TW1257	宮粉羊蹄甲	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
728	6103	TW1258	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	-	-	-	-	-	-	Missing
729	6103	TW1259	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
730	6103	TW1260	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
731	6103	TW1261	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
732	6103	TW1262	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
733	6103	TW1263	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	

734	6103	TW1264	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
735	6103	TW1265	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
736	6103	TW1266	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	25-Aug-10	-	-	-	-	
737	6103	TW1267	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
738	6103	TW1268	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	24-Nov-10	-	-	-	-	Night Work
739	6103	TW1269	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
740	6103	TW1270	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	25-Aug-10	-	-	-	-	
741	6103	TW1271	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	23-Aug-10	-	-	-	-	
742	6103	TW1272	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	23-Aug-10	-	-	-	-	
743	6103	TW1273	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	19-Aug-10	-	-	-	-	
744	6103	TW1274	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	23-Aug-10	-	-	-	-	
745	6103	TW1275	大葉合歡	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	25-Aug-10	-	-	-	-	
746	6103	TW1276	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	19-Aug-10	-	-	-	-	
747	6103	TW1277	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	19-Aug-10	-	-	-	-	
748	6103	TW1278	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	19-Aug-10	-	-	-	-	
749	6103	TW1279	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
750	6103	TW1280	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	25-Aug-10	-	-	-	-	
751	6103	TW1281	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	12-Nov-10	-	-	-	-	Night Work
752	6103	TW1282	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
753	6103	TW1283	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
754	6103	TW1284	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
755	6103	TW1285	朴樹	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	25-Aug-10	-	-	-	-	
756	6103	TW1286	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Remove	-	23-Aug-10	-	-	-	-	
757	6103	TW1287	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
758	6103	TW1288	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
759	6103	TW1289	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
760	6103	TW1290	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
761	6103	TW1291	-	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	-	-	-	-	-	-	Missing
762	6103	TW1292	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	24-Nov-10	-	-	-	-	Night Work
763	6103	TW1293	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	24-Nov-10	-	-	-	-	Night Work
764	6103	TW1294	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	24-Nov-10	-	-	-	-	Night Work
765	6103	TW1295	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Fell	Fell	24-Nov-10	-	-	-	-	Night Work
766	6103	TW1296	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
767	6103	TW1297	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
768	6103	TW1298	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
769	6103	TW1299	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
770	6103	TW1300	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
771	6103	TW1301	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
772	6103	TW1302	台灣相思	Tuen Hing Road to TMR near Tsing Hoi Playground	Retain	Retain	-	-	-	-	-	
773	6104	TW1303	宮粉羊蹄甲	Tsing Wu Square Footpath	Transplant	Transplant	N/A	28-Aug-10	28-Aug-10	30-Sep-10	30-Sep-10	Transplanted
774	6104	TW1304	洋紫荊	Tsing Wu Square Footpath	Transplant	Transplant	N/A	28-Aug-10	11-Sep-10	30-Sep-10	30-Sep-10	Transplanted
775	6104	TW1305	宮粉羊蹄甲	Tsing Wu Square Footpath	Transplant	Transplant	N/A	28-Aug-10	28-Aug-10	30-Sep-10	30-Sep-10	Transplanted
776	6104	TW1306	宮粉羊蹄甲	Tsing Wu Square Footpath	Transplant	Transplant	N/A	25-Aug-10	28-Aug-10	02-Oct-10	02-Oct-10	Transplanted
777	6104	TW1307	宮粉羊蹄甲	Tsing Wu Square Footpath	Transplant	Transplant	N/A	25-Aug-10	28-Aug-10	02-Oct-10	02-Oct-10	Transplanted
778	6104	TW1308	宮粉羊蹄甲	Tsing Wu Square Footpath	Transplant	Transplant	N/A	28-Aug-10	28-Aug-10	02-Oct-10	02-Oct-10	Transplanted
779	6107	TW1309	白千層	Castle Peak Road J/O Tuen Hing Road	Transplant	Transplant	N/A	22-Nov-10	28-Dec-10	Not Yet	Not Yet	
780	6107	TW1310	白千層	Castle Peak Road J/O Tuen Hing Road	Transplant	Transplant	N/A	22-Nov-10	23-Dec-10	Not Yet	Not Yet	
781	6107	TW1311	白千層	Castle Peak Road J/O Tuen Hing Road	Transplant	Transplant	N/A	22-Nov-10	28-Dec-10	Not Yet	Not Yet	
782	6107	TW1312	白千層	Castle Peak Road J/O Tuen Hing Road	Transplant	Transplant	N/A	22-Nov-10	28-Dec-10	Not Yet	Not Yet	
783	6107	TW1313	朴樹	Castle Peak Road J/O Tuen Hing Road	Retain	Retain	-	-	-	-	-	

784	6107	TW1315	朴樹	Castle Peak Road J/O Tuen Hing Road	Transplant	Retain	-	-	-	-	-	
785	6107	TW1316	檸檬桉	Castle Peak Road J/O Tuen Hing Road	Retain	Retain	-	-	-	-	-	
786	6107	TW1340	鳳凰木	Castle Peak Road J/O Tuen Hing Road	Retain	Retain	-	-	-	-	-	
787	6107	TW1341	鳳凰木	Castle Peak Road J/O Tuen Hing Road	Retain	Retain	-	-	-	-	-	
788	6103	TW1369	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	30-Nov-10	30-Nov-10	05-Jan-11	26-Feb-11	Night Work
789	6103	TW1370	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	30-Nov-10	30-Nov-10	05-Jan-11	26-Feb-11	Night Work
790	6103	TW1371	台灣相思	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Fell	Fell	27-Aug-10	-	-	-	-	
791	6103	TW1372	台灣相思	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Fell	Fell	01-Dec-10	-	-	-	-	
792	6103	TW1373	宮粉羊蹄甲	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	02-Dec-10	05-Jan-11	26-Feb-11	Night Work
793	6103	TW1374	台灣相思	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Fell	Fell	27-Aug-10	-	-	-	-	
794	6103	TW1381	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	30-Nov-10	30-Nov-10	31-Dec-10	01-Mar-11	Night Work
795	6103	TW1382	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	30-Nov-10	30-Nov-10	31-Dec-10	01-Mar-11	Night Work
796	6103	TW1383	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	01-Dec-10	31-Dec-10	03-Mar-11	Night Work
797	6103	TW1384	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	01-Dec-10	31-Dec-10	02-Mar-11	Night Work
798	6103	TW1385	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	01-Dec-10	31-Dec-10	02-Mar-11	Night Work
799	6103	TW1386	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	02-Dec-10	31-Dec-10	03-Mar-11	Night Work
800	6103	TW1387	白千層	Tuen Fat Road to Tuen Mun Road near Tuen Lee Street	Transplant	Transplant	N/A	01-Dec-10	02-Dec-10	29-Dec-10	04-Mar-11	Night Work
801	6102	TW1414	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	25-Sep-10	23-Dec-10	01-May-11	Night Work
802	6102	TW1415	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	25-Sep-10	12-Feb-11	Not Yet	17-Dec-10
803	6102	TW1416	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	25-Sep-10	16-Dec-11	01-May-11	Night Work
804	6102	TW1417	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	25-Sep-10	17-Dec-10	01-May-11	Night Work
805	6102	TW1418	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	25-Sep-10	16-Dec-10	01-May-11	Night Work
806	6102	TW1419	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	27-Sep-10	23-Dec-10	Not Yet	
807	6102	TW1420	鳳凰木	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	13-Feb-11	15-Feb-11	09-Apr-11	Not Yet	Big tree crown
808	6102	TW1421	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
809	6102	TW1422	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	28-Sep-10	04-Dec-10	04-Dec-10	Transplanted
810	6102	TW1423	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	18-Sep-10	-	-	-	-	
811	6101	TW1425	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	14-Dec-10	17-Dec-10	19-Jan-11	Not Yet	
812	6101	TW1426	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	17-Dec-10	19-Jan-11	14-Feb-11	27/9 First Root
813	6101	TW1427	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	14-Dec-10	17-Dec-10	19-Jan-11	14-Feb-11	Transplanted
814	6101	TW1428	鳳凰木	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	14-Dec-10	16-Dec-10	19-Jan-11	12-Feb-11	Transplanted
815	6101	TW1429	藍花楹	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	27-Sep-10	04-Dec-10	04-Dec-10	Transplanted
816	6101	TW1430	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	27-Sep-10	03-Dec-10	03-Dec-10	Transplanted
817	6101	TW1431	串錢柳	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	27-Sep-10	03-Dec-10	03-Dec-10	Transplanted
818	6101	TW1432	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
819	6101	TW1433	大葉合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
820	6101	TW1434	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	18-Sep-10	28-Sep-10	17-Dec-10	11-Feb-11	Transplanted
821	6101	TW1435	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
822	6101	TW1436	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
823	6101	TW1437	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
824	6101	TW1438	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	28-Sep-10	-	-	-	-	Night Work
825	6101	TW1439	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Remove	-	-	-	-	-	-	
826	6101	TW1440	血桐	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	27-Sep-10	23-Dec-10	14-Feb-11	Transplanted
827	6101	TW1441	大葉合歡	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	27-Sep-10	16-Dec-10	18-Jan-11	Transplanted
828	6101	TW1442	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	14-Dec-10	16-Dec-10	20-Jan-11	12-Feb-11	Transplanted
829	6101	TW1443	蒲葵	Tuen Mun Road B Bound Slip Road to Pui To Road	Retain	Retain	-	-	-	-	-	
830	6101	TW1444	石栗	Tuen Mun Road B Bound Slip Road to Pui To Road	Retain	Retain	-	-	-	-	-	
831	6101	TW1445	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	25-Sep-10	16-Dec-10	19-Feb-11	Transplanted
832	6101	TW1446	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	25-Sep-10	16-Dec-10	19-Feb-11	Transplanted
833	6101	TW1447	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	24-Sep-10	16-Dec-10	19-Feb-11	Transplanted

834	6101	TW1448	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	19-Feb-11	17-Sep-10	25-Sep-10	16-Dec-10	-	Poor Health
835	6101	TW1449	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
836	6101	TW1450	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	25-Sep-10	16-Dec-10	21-Feb-11	Transplanted
837	6101	TW1451	大葉桉	Tuen Mun Road B Bound Slip Road to Pui To Road	Fell	Fell	25-Sep-10	-	-	-	-	Night Work
838	6101	TW1452	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	N/A	17-Sep-10	25-Sep-10	16-Dec-10	21-Feb-11	Transplanted
839	6101	TW1453	假檳榔	Tuen Mun Road B Bound Slip Road to Pui To Road	Transplant	Transplant	06-Oct-10	-	-	-	-	Poor Health
840	6101	TW1456	-	Tuen Mun Road B Bound Slip Road to Pui To Road	Remove	-	-	-	-	-	-	
841	6101	TW1457	大葉桉	Yan Oi Tong Circuit Car Park	Fell	Fell	16-Nov-10	-	-	-	-	
842	6101	TW1458	大葉桉	Yan Oi Tong Circuit Car Park	Fell	Fell	16-Nov-10	-	-	-	-	
843	6101	TW1459	-	Yan Oi Tong Circuit Car Park	Fell	-	16-Nov-10	-	-	-	-	
844	6101	TW1460	石栗	Yan Oi Tong Circuit Car Park	Fell	Fell	16-Nov-10	-	-	-	-	
845	6101	TW1461	石栗	Yan Oi Tong Circuit Car Park	Fell	Fell	16-Nov-10	-	-	-	-	
846	6101	TW1462	石栗	Yan Oi Tong Circuit Car Park	Fell	Fell	-	-	-	-	-	by other
847	6101	TW1466	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
848	6101	TW1467	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
849	6101	TW1468	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
850	6101	TW1469	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
851	6101	TW1470	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
852	6101	TW1471	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
853	6101	TW1472	白千層	Centre Median near San Tsing Street	Fell	Fell	05-Oct-10	-	-	-	-	
854	6101	TW1473	白千層	Centre Median near San Tsing Street	Retain	Retain	-	-	-	-	-	
855	6101	TW1474	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
856	6101	TW1475	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
857	6101	TW1476	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
858	6101	TW1477	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
859	6101	TW1478	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
860	6101	TW1479	白千層	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
861	6101	TW1480	黃花夾竹桃	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
862	6101	TW1481	黃花夾竹桃	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
863	6101	TW1482	黃花夾竹桃	San Tsing Street Car Park	Retain	Retain	-	-	-	-	-	
864	6108	TW1526	檸檬桉	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
865	6108	TW1527	檸檬桉	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
866	6108	TW1528	檸檬桉	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
867	6108	TW1529	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
868	6108	TW1530	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
869	6108	TW1531	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
870	6108	TW1532	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
871	6108	TW1533	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
872	6108	TW1534	檸檬桉	Castle Peak Road J/O Fu Fat Lane	Fell	Fell	Not Yet	-	-	-	-	
873	6108	TW1535	石栗	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
874	6108	TW1536	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
875	6108	TW1537	木棉	Castle Peak Road J/O Fu Fat Lane	Transplant	Transplant	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
876	6108	TW1538	洋紫荊	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	Not Yet	Not Yet	Not Yet	
877	6108	TW1539	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	Not Yet	Not Yet	Not Yet	
878	6108	TW1540	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	Not Yet	Not Yet	Not Yet	
879	6108	TW1541	洋紫荊	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	02-Apr-11	Not Yet	Not Yet	
880	6108	TW1542	洋紫荊	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	02-Apr-11	Not Yet	Not Yet	
881	6108	TW1543	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	01-Apr-11	Not Yet	Not Yet	
882	6108	TW1544	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	01-Apr-11	Not Yet	Not Yet	
883	6108	TW1545	洋紫荊	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	02-Apr-11	Not Yet	Not Yet	

884	6108	TW1546	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	01-Apr-11	Not Yet	Not Yet	
885	6108	TW1547	宮粉羊蹄甲	Castle Peak Road near Fu Fat Lane Footpath	Transplant	Transplant	N/A	19-Nov-10	01-Apr-11	Not Yet	Not Yet	
886	6108	TW1548	白千層	Castle Peak Road near Fu Fat Lane Footpath	Fell	Fell	Not Yet	-	-	-	-	
887	6108	TW1549	木麻黃	Castle Peak Road near Fu Fat Lane Footpath	Fell	Fell	Not Yet	-	-	-	-	
888	6108	TW1550	木麻黃	Castle Peak Road near Fu Fat Lane Footpath	Fell	Fell	Not Yet	-	-	-	-	
889	6108	TW1551	木麻黃	Castle Peak Road near Fu Fat Lane Footpath	Fell	Fell	Not Yet	-	-	-	-	
890	6108	TW1552	木麻黃	Castle Peak Road near Fu Fat Lane Footpath	Fell	Fell	Not Yet	-	-	-	-	
891	6105	TW1553	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	21-Sep-10	21-Sep-10	Transplanted
892	6105	TW1554	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	17-Aug-10	17-Aug-10	21-Sep-10	21-Sep-10	Transplanted
893	6105	TW1555	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	21-Sep-10	21-Sep-10	Transplanted
894	6105	TW1556	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
895	6105	TW1557	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
896	6105	TW1558	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
897	6105	TW1559	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
898	6105	TW1560	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
899	6105	TW1561	串錢柳	Tsing Sin Playground	Transplant	Transplant	N/A	18-Aug-10	18-Aug-10	20-Sep-10	20-Sep-10	Transplanted
900	6105	TW1562	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	25-Aug-10	Transplanted
901	6105	TW1563	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	25-Aug-10	Transplanted
902	6105	TW1564	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	25-Aug-10	Transplanted
903	6105	TW1565	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	25-Aug-10	Transplanted
904	6105	TW1566	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	24-Aug-10	Transplanted
905	6105	TW1567	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	24-Aug-10	Transplanted
906	6105	TW1568	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	24-Aug-10	Transplanted
907	6105	TW1569	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	24-Aug-10	Transplanted
908	6105	TW1570	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	25-Aug-10	Transplanted
909	6105	TW1571	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	25-Aug-10	Transplanted
910	6105	TW1572	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	25-Aug-10	Transplanted
911	6105	TW1573	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	25-Aug-10	Transplanted
912	6105	TW1574	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	26-Aug-10	Transplanted
913	6105	TW1575	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	26-Aug-10	Transplanted
914	6105	TW1576	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	26-Aug-10	Transplanted
915	6105	TW1577	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	26-Aug-10	Transplanted
916	6105	TW1578	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	26-Aug-10	Transplanted
917	6105	TW1579	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	26-Aug-10	Transplanted
918	6105	TW1580	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	04-Aug-10	04-Aug-10	04-Aug-10	26-Aug-10	Transplanted
919	6105	TW1581	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
920	6105	TW1582	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
921	6105	TW1583	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
922	6105	TW1584	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
923	6105	TW1585	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
924	6105	TW1586	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
925	6105	TW1587	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
926	6105	TW1588	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
927	6105	TW1589	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
928	6105	TW1590	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
929	6105	TW1591	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
930	6105	TW1592	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
931	6105	TW1593	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	26-Aug-10	Transplanted
932	6105	TW1594	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	27-Aug-10	Transplanted
933	6105	TW1595	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	05-Aug-10	05-Aug-10	05-Aug-10	27-Aug-10	Transplanted

[illegible]

984	6105	TW1646	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	14-Sep-10	Transplanted
985	6105	TW1647	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	14-Sep-10	Transplanted
986	6105	TW1648	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	14-Sep-10	Transplanted
987	6105	TW1649	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	14-Sep-10	Transplanted
988	6105	TW1650	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	14-Sep-10	Transplanted
989	6105	TW1651	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	14-Sep-10	Transplanted
990	6105	TW1652	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	14-Sep-10	Transplanted
991	6105	TW1653	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	14-Sep-10	Transplanted
992	6105	TW1654	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	13-Sep-10	Transplanted
993	6105	TW1655	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	13-Sep-10	Transplanted
994	6105	TW1656	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	13-Sep-10	Transplanted
995	6105	TW1657	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	13-Sep-10	Transplanted
996	6105	TW1658	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	13-Sep-10	Transplanted
997	6105	TW1659	散尾葵	Tsing Sin Playground	Transplant	Transplant	N/A	03-Aug-10	03-Aug-10	03-Aug-10	13-Sep-10	Transplanted
998	6108	TWA1	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
999	6108	TWA2	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1000	6108	TWA3	石栗	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1001	6108	TWA4	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1002	6108	TWA5	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1003	6108	TWA6	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1004	6108	TWA7	白千層	Castle Peak Road J/O Fu Fat Lane	Fell	-	Not Yet	-	-	-	-	
1005	6108	TWA8	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1006	6108	TWA9	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1007	6108	TWA10	石栗	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1008	6108	TWA11	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1009	6108	TWA12	白千層	Castle Peak Road J/O Fu Fat Lane	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1010	6109	TWA30	火焰木	Castle Peak Road - Castle Peak Bay Outside Site Office	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1011	6109	TWA31	火焰木	Castle Peak Road - Castle Peak Bay Outside Site Office	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1012	6109	TWA32	木棉	Castle Peak Road - Castle Peak Bay Outside Site Office	Transplant	-	N/A	Not Yet	Not Yet	Not Yet	Not Yet	
1013	6101	TWA33	鳳凰木	Yan Oi Tong Circuit Car Park	Fell	-	14-Mar-11	-	-	-	-	
1014	6101	TWA34	洋蹄甲	Yan Oi Tong Circuit Car Park	Fell	-	14-Mar-11	-	-	-	-	
1015	6101	TWA35	蒲葵	Yan Oi Tong Circuit Car Park	Transplant	-	N/A	14-Mar-11	15-Apr-11	Not Yet	Not Yet	
1016	6101	TWA36	蒲葵	Yan Oi Tong Circuit Car Park	Transplant	-	N/A	14-Mar-11	15-Apr-11	Not Yet	Not Yet	
1017	6104	TWA37	洋蹄甲	Tsing Wui Street Car Park	Fell	-	14-Mar-11	-	-	-	-	
1018	6104	TWA38	火焰木	Tsing Wui Street Car Park	Transplant	-	N/A	14-Mar-11	31-Mar-11	Not Yet	Not Yet	
1019	6103	TWA39	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	-	13-Mar-11	-	-	-	-	Night Work
1020	6103	TWA40	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	-	13-Mar-11	-	-	-	-	Night Work
1021	6103	TWA41	宮粉羊蹄甲	Tuen Mun Road Slip Road to Tuen Hing Road	Fell	-	13-Mar-11	-	-	-	-	Night Work

24 nos. of New trees under UPTRA No.1 & Revised the proposed treatment

26 nos. of big crown trees

29 nos. of trees in poor health (Application No.2)

Appendix J

**Monthly Summary
Waste Flow Table**



Monthly Summary of Waste Flow Table for 2011 (year)

Name of Person completing the Record: Marko Chan

Month	Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(see Note 1) (in '000m ³)						(see Note 2) (in '000 Kg)		
Jan	0.536250	Nil	Nil	Nil	0.536250	0.00300	0.35000	Nil	Nil	0.053630
Feb	1.823250	Nil	0.053625	Nil	1.769625	0.10211	Nil	Nil	Nil	0.039000
Mar	2.676375	Nil	Nil	Nil	2.676375	2.40500	Nil	Nil	Nil	0.102375
Apr	6.490960	Nil	Nil	Nil	6.490960	2.72000	Nil	Nil	Nil	0.047010
May										
Jun										
Sub-total	11.526835	Nil	0.053625	Nil	11.473210	5.23011	0.35000	Nil	Nil	0.242015
Jul										
Aug										
Sept										
Oct										
Nov										
Dec										
Total										

Notes:

- (1) Broken concrete for recycling into aggregates.
- (2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- (3) Use the conversion factor: 1 full load of dumping truck being equivalent to 6.5m³ by volume.

Appendix K

**Environmental
Monitoring Programme
for Coming Month**

Agreement No. CE 22/2005 (HY) Traffic Improvement to Tuen Mun Road Town Centre Section
Tentative Impact Monitoring Schedule - May 2011 Revision 1

Date		Air Quality	Noise	Landscape & Visual	Site Inspection
		24-hours TSP	L _{Aeq} , 30 min		
1-May-11	Sun				
2-May-11	Mon				
3-May-11	Tue				
4-May-11	Wed				
5-May-11	Thu				
6-May-11	Fri				
7-May-11	Sat				
8-May-11	Sun				
9-May-11	Mon				
10-May-11	Tue				
11-May-11	Wed				
12-May-11	Thu				SSEMC
13-May-11	Fri				
14-May-11	Sat				
15-May-11	Sun				
16-May-11	Mon				
17-May-11	Tue				
18-May-11	Wed				
19-May-11	Thu				
20-May-11	Fri				
21-May-11	Sat				
22-May-11	Sun				
23-May-11	Mon				
24-May-11	Tue				
25-May-11	Wed				
26-May-11	Thu				
27-May-11	Fri				
28-May-11	Sat				
29-May-11	Sun				
30-May-11	Mon				
31-May-11	Tue				

	Public Holiday
	Monitoring Day

Monitoring Details

Monitoring	Quantity	Locations	Parameters
Air Quality	6	Mrs.Aw Boon Haw Secondary School Tai Tung Pui Social Service Building Wu Siu Kui Primary School Choi Cheung Kok Secondary School Tuen Mun Town Hall Yan Oi Tong Community and Sport Centre	24-hour TSP, Wind speed / direction
Noise	6	Kam Fai Garden Tai Tung Pui Social Service Building Yuen Yuen Primary School Wu Siu Kui Primary School Tuen King Building Choi Cheung Kok Secondary School	L _{Aeq} (30 min), L ₁₀ , L ₉₀

Appendix L

Complaint Log

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Complaint Log

ET's Complaint Log Ref. no.	Incoming Complaint Ref no.	Name of Complainant	Date of Complaint receive	Complaint Date/ Period	Complaint Location	Area of Concern	Details of Complaint	Date of Complaint received by ET	ET's Investigation Date	Investigation / Mitigation Measures	Validity to the Project	Status
C003-TCS	Three complaints regarding same issue were received by ICC on 1, 3 and 4 April 11 respectively and the Supervising Officer Representative was informed via the e-mail on same date.	Unknown	1, 3 and 4 Apr 11	Evening time of 1 Apr 11	Muddy water spillage on TMR in the vicinity of Tuen Mun Town Plaza (near Tuen Hi Road)	Water quality	Three complaints were related to muddy water spillage on TMR in the vicinity of Tuen Mun Town Plaza (near Tuen Hi Road)	4 April 11	7 ~ 15 Apr 11	<p>As confirmed by the Contractor and Supervising Officer's Representative, muddy water was overflowed to Tuen Mun Road (Yuen Long bound) in the vicinity of Tuen Mun Town Plaza (near Tuen Hi Road) on 1 Apr 11 evening time.</p> <p>Based on the information provided by the Contractor and Supervising Officer's Representative, the overflow of muddy spillage was anticipated to be from the broken hose to direct the pump to the wastewater treatment facility. Immediate actions were taken by the Contractor for ceasing the pump and cleaning of muddy spillage. It is therefore concluded that the complaint was work-related under the Project.</p> <p>The site inspection was carried on 7 and 14 Apr 11, the damaged hose had been replaced and the condition was satisfactory. No abnormal operation was observed.</p> <p>Nevertheless, it is recommended that the Contractor should undertake following mitigation measures to minimize the noise nuisance.</p> <ol style="list-style-type: none"> 1. Inspect the conditions of the hoses and connections daily; 2. Well-maintain the hoses and connections condition and replace the old/damaged hoses and connections if necessary; 3. Relocate the hoses as far as possible from the machines and construction materials to minimize the possibility of damage; 4. Stock the spare pumps, hoses and connections on-site for immediate action in case of spillage occurs; 5. Provide adequate bunding along the site boundary to minimize the possibility of the muddy water overflowing to public area in case of spillage occurs; and 6. Enhance the workers awareness by regular training to handle the muddy water spillage incident. 	Yes	Closed on 16 Apr 11

Agreement No. HMW 5/2009 (EP) Traffic Improvements to Tuen Mun Road Town Centre Section
Complaint Log

ET's Complaint Log Ref. no.	Incoming Complaint Ref no.	Name of Complainant	Date of Complaint receive	Complaint Date/ Period	Complaint Location	Area of Concern	Details of Complaint	Date of Complaint received by ET	ET's Investigation Date	Investigation / Mitigation Measures	Validity to the Project	Status
C004-TCS	Four complaints regarding same issue were received by ICC on 18, 21 and 28 April 11 respectively and the Supervising Officer Representative was informed via the e-mail on same date.	Unknown	<ul style="list-style-type: none"> 18 Apr 11 (1 complaint from Chi Lok Fa Yuen), 21 Apr 11 (1 complaint from Tuen Mun Fa Yuen) and 28 Apr (two complaints from Waldorf Garden and Tuen Mun Park Lane Square separately) 	Restricted hours (night time and Sunday) between 17 and 28 Apr 11	TMR in the vicinity of Chi Lok Fa Yuen, Tuen Mun Fa Yuen, Waldorf Garden and Tuen Mun Park Lane Square	Noise	Four complaints were related to noise nuisance on TMR during the restricted hours (night time and Sunday)	4 May 11	5 ~ 15 May 11	<p>As confirmed by the Contractor and Supervising Officer's Representative, the loading and unloading works at central median was carried out on TMR during the complaint period in the vicinity of Chi Lok Fa Yuen, Tuen Mun Fa Yuen, Waldorf Garden and Tuen Mun Park Lane Square.</p> <p>Totally 3 units of power mechanical equipments had been used including lorry, dump truck and excavator. The relevant construction noise permit (CNP) no. GW-RW0640-10 was obtained for the above works prior commencement. The conditions stipulated in the CNP were strictly followed by the Contractor. EPD had been informed prior the work commencement.</p> <p>Based on the above-mentioned information provided by the Contractor, it is anticipated that the noise nuisance was mainly due to the machines operation. Therefore, it is concluded that the complaint was work-related under the Project.</p> <p>In accordance with the Action/Event Plan, additional noise monitoring during the restricted hours was undertaken on 6 May 11 at the monitoring location N5 (Tuen King Building) and N6 (The Chinese Manufacturers' Association of Hong Kong Choi Cheung Kok Secondary School), where the loading and unloading works was carried out on TMR during restricted hours (night time) in the vicinity of these two monitoring locations.</p> <p>Comparison is made between the monitoring results against the corresponding baseline noise level. Based on the interpretation from the results, the construction noise at both locations are 54dB(A) which below the night time noise limit level (55dB(A)).</p> <p>Nevertheless, ET recommended that the Contractor should undertake following mitigation measures to minimize the noise nuisance.</p> <ol style="list-style-type: none"> 1. Minimize the no. of machines used for the work as far as possible; 2. Well-maintain the machines condition to minimize noise nuisance; 3. Relocate operating machinery as far as possible from nearby sensitive receivers; 4. Machines that may be in intermittent use should be shut down between work periods or should be throttled down; 5. Optimize the working programme to minimize the restricted hours work activities as far as possible; 6. Improve the working practices to minimize the noise nuisance during the working activities as far as possible; 7. Provide temporary / mobile noise barrier for the noisy activities as far as possible; and 8. Enhance the workers awareness by regular training to minimize noise nuisance during the restricted hours. 	Yes	Closed on 16 May 11
