

Civil Engineering and Development Department

**Agreement No. CE 59/2015 (EP)
Environmental Team for
Tseung Kwan O – Lam Tin Tunnel
Design and Construction**

**Monthly Environmental Monitoring and
Audit Report for October 2017**

(version 1.0)

Approved By



(Dr. Priscilla Choy,
Environmental Team Leader)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties.

CINOTECH CONSULTANTS LTD

Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong
Tel: (852) 2151 2083 Fax: (852) 3107 1388
Email: info@cinotech.com.hk

TABLE OF CONTENTS

| | |
|--|-----------|
| EXECUTIVE SUMMARY | 1 |
| Introduction | 1 |
| Environmental Monitoring Works | 1 |
| Key Information in the Reporting Month | 3 |
| Key Construction Activities in the Reporting Month | 3 |
| Future Key Issues | 4 |
| 1. INTRODUCTION | 6 |
| Purpose of the Report..... | 6 |
| Structure of the Report..... | 6 |
| 2. PROJECT INFORMATION | 8 |
| Background | 8 |
| Project Organizations | 8 |
| Construction Activities undertaken during the Reporting Month..... | 9 |
| Status of Environmental Licences, Notification and Permits | 10 |
| Summary of EM&A Requirements..... | 12 |
| 3. AIR QUALITY | 13 |
| Monitoring Requirements | 13 |
| Monitoring Locations..... | 13 |
| Monitoring Equipment..... | 13 |
| Monitoring Parameters and Frequency | 14 |
| Monitoring Methodology..... | 14 |
| Results and Observations | 17 |
| 4. NOISE | 18 |
| Monitoring Requirements | 18 |
| Monitoring Locations..... | 18 |
| Monitoring Equipments | 18 |
| Monitoring Methodology and QA/QC Procedure | 19 |
| Results and Observations | 20 |
| Updated Construction Noise Assessment | 20 |
| 5. WATER QUALITY | 21 |
| Monitoring Requirements | 21 |
| Monitoring Locations..... | 21 |
| Monitoring Equipments | 22 |
| Monitoring Parameters and Frequency | 24 |
| Monitoring Methodology..... | 24 |
| Laboratory Analytical Methods | 25 |
| QA/QC Requirements | 26 |
| Results and Observations | 26 |
| 6. ECOLOGY | 28 |
| Post-Translocation Coral Monitoring | 28 |
| Event and Action Plan..... | 28 |
| Results and Observations | 28 |
| 7. CULTURAL HERITAGE | 29 |

| | |
|--|-----------|
| Monitoring Requirement | 29 |
| Monitoring Locations | 29 |
| Monitoring Equipment | 29 |
| Monitoring Methodology | 30 |
| Alert, Alarm and Action Levels | 30 |
| Results | 30 |
| Mitigation Measures for Cultural Heritage | 31 |
| 8. LANDSCAPE AND VISUAL IMPACT REQUIREMENTS | 32 |
| 9. LANDFILL GAS MONITORING | 33 |
| Monitoring Requirement | 33 |
| Monitoring Parameters and Frequency | 33 |
| Monitoring Locations | 33 |
| Monitoring Equipment | 33 |
| Results and Observations | 34 |
| 10. ENVIRONMENTAL AUDIT | 35 |
| Site Audits | 35 |
| Implementation Status of Environmental Mitigation Measures | 35 |
| 11. WASTE MANAGEMENT | 36 |
| 12. ENVIRONMENTAL NON-CONFORMANCE | 37 |
| Summary of Exceedances | 37 |
| Summary of Environmental Non-Compliance | 37 |
| Summary of Environmental Complaint | 37 |
| Summary of Environmental Summon and Successful Prosecution | 37 |
| 13. FUTURE KEY ISSUES | 38 |
| Key Issues for the Coming Month | 39 |
| Monitoring Schedule for the Next Month | 39 |
| 14. CONCLUSIONS AND RECOMMENDATIONS | 40 |
| Conclusions | 40 |
| Recommendations | 41 |

LIST OF TABLES

| | |
|------------|---|
| Table I | Non-compliance (exceedance) Recorded for the Project in the Reporting Month |
| Table II | Summary Table for Key Information in the Reporting Month |
| Table III | Summary Table for Major Site Activities in the Reporting Month |
| Table IV | Summary Table for Site Activities in the next Reporting Period |
| Table 2.1 | Key Project Contacts |
| Table 2.2 | Summary Table for Major Site Activities in the Reporting Month |
| Table 2.3 | Construction Programme Showing the Inter-Relationship with Environmental Protection/Mitigation Measures |
| Table 2.4 | Summary of the Status of Environmental Licences, Notification and Permits |
| Table 3.1 | Locations for Air Quality Monitoring |
| Table 3.2 | Air Quality Monitoring Equipment |
| Table 3.3 | Impact Dust Monitoring Parameters, Frequency and Duration |
| Table 3.4 | Major Dust Source during Air Quality Monitoring |
| Table 4.1 | Noise Monitoring Stations |
| Table 4.2 | Noise Monitoring Equipment |
| Table 4.3 | Noise Monitoring Parameters, Frequency and Duration |
| Table 4.4 | Major Noise Source during Noise Monitoring |
| Table 4.5 | Baseline Noise Level and Noise Limit Level for Monitoring Stations |
| Table 5.1 | Groundwater Quality Monitoring Stations |
| Table 5.2 | Marine Water Quality Monitoring Stations |
| Table 5.3 | Water Quality Monitoring Equipment |
| Table 5.4 | Water Quality Monitoring Parameters and Frequency |
| Table 5.5 | Methods for Laboratory Analysis for Water Samples |
| Table 5.6 | Summary of Groundwater Quality Monitoring Results |
| Table 6.1 | Location and Physical attributes of the Coral Recipient Site |
| Table 7.1 | Vibration Monitoring Equipment |
| Table 7.2 | AAA Levels for Monitoring for Cultural Heritage |
| Table 7.3 | Vibration Monitoring Results |
| Table 9.1 | Landfill Gas Monitoring Equipment |
| Table 13.1 | Summary Table for Site Activities in the next Reporting Period |

LIST OF FIGURES

| | |
|-----------|---|
| Figure 1 | Site Layout Plan |
| Figure 1a | Site Portions under Works Contract No. NE/2015/02 |
| Figure 2 | Locations of Air Quality Monitoring Stations |
| Figure 3 | Locations of Construction Noise Monitoring Stations |
| Figure 4 | Locations of Groundwater Quality Monitoring Stations |
| Figure 5 | Locations of Marine Water Quality Monitoring Stations |
| Figure 6 | Locations of Landfill Gas Monitoring |
| Figure 7 | Location of Post-translocation Coral Monitoring |
| Figure 8 | Location of Monitoring for Cultural Heritage |

LIST OF APPENDICES

- Appendix A Action and Limit Levels
- Appendix B Copies of Calibration Certificates
- Appendix C Weather Information
- Appendix D Environmental Monitoring Schedules
- Appendix E 1-hour TSP Monitoring Results and Graphical Presentations
- Appendix F 24-hour TSP Monitoring Results and Graphical Presentations
- Appendix G Noise Monitoring Results and Graphical Presentations
- Appendix H Groundwater Quality Monitoring Results, Graphical Presentations and Laboratory Testing Reports
- Appendix I Marine Water Quality Monitoring Results and Graphical Presentations
- Appendix J Quality Control Reports for Laboratory Analysis
- Appendix K Summary of Exceedance
- Appendix L Site Audit Summary
- Appendix M Event and Action Plans
- Appendix N Implementation Schedule And Recommended Mitigation Measures
- Appendix O Summaries of Environmental Complaint, Warning, Summon and Notification of Successful Prosecution
- Appendix P Waste Generation in the Reporting Month
- Appendix Q Tentative Construction Programme
- Appendix R Record of Landfill Gas Monitoring by Contractor
- Appendix S Updated Construction Noise Assessment
- Appendix T Photo record of Post-Translocation Coral Monitoring Survey

EXECUTIVE SUMMARY

Introduction

1. This is the 12th Environmental Monitoring and Audit (EM&A) Report prepared by Cinotech Consultants Limited for the “Agreement No. CE 59/2015 (EP) Environmental Team for Tseung Kwan O – Lam Tin Tunnel – Design and Construction” (hereinafter called “the Project”). This report documents the findings of EM&A Works conducted in October 2017.
2. During the reporting month, the following works contracts were undertaken:
 - Contract No. NE/2015/01 – Tseung Kwan O – Lam Tin Tunnel – Main Tunnel and Associated Works;
 - Contract No. NE/2015/02 – Tseung Kwan O – Lam Tin Tunnel – Road P2 and Associated Works;
 - Contract No. NE/2015/03 – Tseung Kwan O – Lam Tin Tunnel – Northern Footbridge.

Environmental Monitoring Works

3. Environmental monitoring for the Project was performed in accordance with the EM&A Manual and the monitoring results were checked and reviewed. Site Inspections/Audits were conducted once per week. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.
4. Summary of the non-compliance (exceedance) in the reporting month for the Project is tabulated in **Table I**.

Table I Non-compliance (exceedance) Record for the Project in the Reporting Month

| Environmental Monitoring | No. of Non-compliance (Exceedance) | | No. of Non-compliance (Exceedance) due to Construction Activities of this Project | | Action Taken |
|--|------------------------------------|-------------|---|-------------|--|
| | Action Level | Limit Level | Action Level | Limit Level | |
| Air Quality | 0 | 0 | 0 | 0 | N/A |
| Noise | 5 | 1 | 4 | 1 | Refer to the Appendix O |
| Groundwater Quality | 1 | 0 | 0 | 0 | N/A (Refer to Part 8, Executive Summary) |
| Marine Water Quality | 0 | 0 | 0 | 0 | N/A |
| Groundwater Level Monitoring (Piezometer Monitoring) | N/A | N/A | N/A | N/A | N/A |
| Ecological | N/A | N/A | N/A | N/A | N/A |
| Cultural Heritage | 0 | 0 | 0 | 0 | N/A |
| Landfill Gas | 0 | 0 | 0 | 0 | N/A |

Air Quality Monitoring

5. All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

6. All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

Construction Noise Monitoring

7. All noise monitoring was conducted as scheduled in the reporting month. Four Action Level exceedance was recorded due to the documented complaints received in the reporting month. One Limit Level exceedance was recorded in the reporting month.

Water Quality Monitoring

8. Groundwater monitoring was conducted as scheduled in the reporting month. One Action Level exceedance was recorded in the reporting month which is considered to be non-Project related.
9. All marine water monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
10. Construction phase daily piezometer monitoring was not carried out in this reporting period as there is no tunnel construction activities are carried out within +/- 50m of the piezometer gate in plan.

Ecological Monitoring

11. Post-translation coral monitoring survey shall be conducted once every 3 months for a period of 12 months after completion of coral translocation. The 4th post-translocation coral monitoring survey is scheduled in November 2017.

Monitoring on Cultural Heritage

12. Monitoring of impacts on Cultural Heritage at Cha Kwo Ling Tin Hau Temple commenced in April 2017. No Alert Alarm and Action (AAA) Level exceedance was recorded in the reporting month.

Landscape and Visual Monitoring and Audit

13. The implementation of landscape and visual mitigation measures was checked during the environmental site inspections. Recommended follow-up actions have been discharged by the Contractor. Details of the audit findings and implementation status are presented in Section 10.

Landfill Gas Monitoring

14. Monitoring of landfill gases commenced in December 2016 and were carried out by the Contractor at excavation location, Portion III. No Limit Level exceedance was recorded.

Environmental Site Inspection

15. Joint weekly site inspections were conducted by representatives of the Contractor, Engineer and Environmental Team. The representative of the IEC joined the site inspection for NE/2015/01, NE/2015/02 and NE/2015/03 on 25, 26, 09 October 2017

respectively. Details of the audit findings and implementation status are presented in Section 10.

Waste Management

16. Wastes generated from this Project include inert construction and demolition (C&D) materials, non-inert C&D materials and marine sediments. Details of waste management data is presented in Section 11 and **Appendix P**.

Key Information in the Reporting Month

17. Summary of key information in the reporting month is tabulated in **Table II**.

Table II Summary Table for Key Information in the Reporting Month

| Event | Event Details | | Action Taken | Status | Remark |
|---|---------------|---|-------------------------|----------|------------------------|
| | Number | Nature | | | |
| Complaint received by Project Team / Complaint referred by EPD (October 2017) | 8 | Construction dust / noise nuisance / Water quality / Landscape and Visual Impacts | Under investigation | On-going | Details refer to App O |
| Complaint received by Project Team / Complaint referred by EPD (September 2017) | 14(*) | Construction dust / noise nuisance / Landscape and Visual Impacts | Under investigation | On-going | |
| Complaint received by Project Team / Complaint referred by EPD (August 2017) | 8 | Muddy water discharge / Landscape and Visual Impacts | Investigation completed | Closed | --- |
| Notifications of any summons & prosecutions received | 0 | --- | N/A | N/A | --- |

Note (*): Previous case received on 26 Sep 2017 on construction noise nuisance in Tseung Kwan O is confirmed to be Enquiry on the Project instead of a documented complaint.

Key Construction Activities in the Reporting Month

18. Summary of key construction activities in the reporting month is tabulated in **Table III**.

Table III Summary Table for Major Site Activities in the Reporting Month

| Contract No. | Project Title | Site Activities (October 2017) | |
|--------------|---|--------------------------------|--|
| NE/2015/01 | Tseung Kwan O – Lam Tin Tunnel – Main Tunnel and Associated Works | Lam Tin Interchange | 1) EHC2 U-Trough 2) Site Formation – Area 1G1, Area 1G2, 2, 3, 4 & Area 5 3) Pipe Pile wall – Area 2A |
| | | Main Tunnel | 1) Main Tunnel Excavation |
| | | TKO Interchange | 1) Haul Road Construction, Site Formation and Slope Works 2) Temporary Barging Facilities & Temporary Platform 3) Temporary Cut Slope For BMCPC 4) Steel Platform for Bridge Construction |

| | | |
|------------|---|--|
| NE/2015/02 | Tseung Kwan O – Lam Tin Tunnel – Road P2 and Associated Works | <ol style="list-style-type: none"> 1) Site Clearance - Removal of vegetation and general refuse in Portion V and VI 2) Hoarding Erection 3) Advance Works for Construction of Steel Cofferdam in Portion VIII and Area Y 4) Reinstatement of Temporary Steel Cofferdam and Double Water Gate 5) Construction of Retaining Wall (Portion VIII and Area Y) 6) Re-provision of DSD transformation room (Portion I) 7) Piling works at Tong Yin Street (Portion VI) 8) Pre-bored works at Portion IV & VII 9) Demolition of Existing Transformer Room (Portion III) |
| NE/2015/03 | Tseung Kwan O – Lam Tin Tunnel – Northern Footbridge | <ol style="list-style-type: none"> 1) Foundation piling at West Pier 2) Pile Cap Construction (with ELS) at East Pier 3) Pile Construction at East Pier |

Future Key Issues

19. The future key environmental issues in the coming month include:

Table IV Summary Table for Site Activities in the next Reporting Period

| Contract No. and Project Title | Site Activities (November 2017) | Key environmental issues * | |
|--|---|---|-----------------------------------|
| NE/2015/01 - Tseung Kwan O - Lam Tin Tunnel - Main Tunnel and Associated Works | Lam Tin Interchange | <ol style="list-style-type: none"> 1) EHC2 U-Trough 2) Site Formation – Area 1G1, Area 1G2, Area 2, Area 3, Area 4 & Area 5 3) Pipe Pile Wall – Area 2A | (A) / (B) / (C) / (D) / (E) |
| | Main Tunnel | <ol style="list-style-type: none"> 1) Main Tunnel Excavation | (B) |
| | TKO Interchange | <ol style="list-style-type: none"> 1) Haul Road Construction and Site Formation & Slope Works 2) Temporary Cut Slope For BMCPC 3) Temporary Barging Facilities & Temporary Platform 4) Steel Platform for Bridge Construction | (A) / (C) / (D) / (E) / (F) / (I) |
| NE/2015/02 - Tseung Kwan O – Lam Tin Tunnel – Road P2 and Associated Works | <ol style="list-style-type: none"> 1) Site Clearance - Removal of vegetation and general refuse in Portion V and VI 2) Hoarding Erection 3) Advance Works for Construction of Steel Cofferdam in Portion VIII and Area Y 4) Reinstatement of Temporary Steel Cofferdam and Double Water Gate 5) Construction of Retaining Wall (Portion VIII and Area Y) 6) Re-provision of DSD transformation room (Portion I) | (A) / (B) / (C) / (D) / (E) / (F) / (G) / (H) / (I) | |

| | | |
|---|---|-----------------|
| | 7) Piling works at Tong Yin Street (Portion VI) 8) Pre-bored works at Portion IV & VII 9) Demolition of Existing Transformer Room (Portion III) | |
| NE/2015/03 - Tseung Kwan O – Lam Tin Tunnel – Northern Footbridge | 1) Pile Construction at East Pier 2) Pile Cap Construction (with ELS) at East Pier | (A) / (C) / (D) |

Note:

- (A) Watering for dust generation from haul road, stockpiles of dusty materials, exposed site area, excavation works and rock breaking activities;
- (B) Noisy construction activity such as rock-breaking activities and piling works;
- (C) Runoff from exposed slope or site area;
- (D) Wastewater and runoff discharge from site;
- (E) Accumulation of silt, mud and sand along U-channels and sedimentation tanks;
- (F) Set up and implementation of temporary drainage system for the surface runoff;
- (G) Storage of chemicals/fuel and chemical waste/waste oil on site;
- (H) Accumulation and storage of general and construction waste on site; and
- (I) Marine water quality impact and indirect impact to coral communities due to marine construction for TKO-LTT reclamation.

1. INTRODUCTION

- 1.1 Cinotech Consultants Limited (Cinotech) was commissioned by Civil Engineering and Development Department (CEDD) as the Environmental Team (ET) to undertake environmental monitoring and auditing services for the Works Contracts involved in the implementation of Tseung Kwan O – Lam Tin Tunnel (TKO-LTT) project to ensure that the environmental performance of the Works Contracts comply with the requirements specified in the Environmental Permit (EP), Environmental Monitoring & Audit (EM&A) Manual, Environmental Impact Assessment (EIA) Report of the TKO-LTT project and other relevant statutory requirements. This is the 12th Monthly EM&A report summarizing the EM&A works for the Project in October 2017.

Purpose of the Report

- 1.2 This is the 12th Monthly EM&A Report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period in October 2017.

Structure of the Report

- 1.3 The structure of the report is as follows:

Section 1: **Introduction** – purpose and structure of the report.

Section 2: **Contract Information** – summarises background and scope of the Contract, site description, project organization and contact details, construction programme, the construction works undertaken and the status of Environmental Permits/Licenses during the reporting month.

Section 3: **Air Quality Monitoring** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, monitoring results and Event / Action Plans.

Section 4: **Noise Monitoring** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, monitoring results and Event / Action Plans.

Section 5: **Water Quality Monitoring** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, monitoring results and Event / Action Plans.

Section 6: **Ecological Monitoring** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations and Action and Limit Levels, monitoring results and Event / Action Plans.

Section 7: **Cultural Heritage** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations and monitoring results.

Section 8: **Landscape and Visual Monitoring Requirements** – summarises the requirements of landscape and visual monitoring

Section 9: **Landfill Gas Monitoring** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, monitoring results and Limit Levels and Action Plan

Section 10: **Environmental Site Inspection** – summarises the audit findings of the weekly site inspections undertaken within the reporting month.

Section 11: **Waste Management** – summarises the waste management data in the reporting month.

Section 12: **Environmental Non-conformance** – summarises any monitoring exceedance, environmental complaints, environmental summons and successful prosecutions within the reporting month.

Section 13: **Future Key Issues** – summarises the impact forecast and monitoring schedule for the next three months.

Section 14: **Conclusions and Recommendation**

2. PROJECT INFORMATION

Background

- 2.1 In 2002, Civil Engineering and Development Department (CEDD) commissioned an integrated planning and engineering study under Agreement No. CE 87/2001 (CE) “Further Development of Tseung Kwan O – Feasibility Study” (the “TKO Study”) to formulate a comprehensive plan for further development of TKO New Town. It recommended to further develop TKO to house a total population of 450,000 besides the district’s continuous commercial and industrial developments.
- 2.2 At present, the Tseung Kwan O Tunnel is the main connection between Tseung Kwan O (TKO) and other areas in the territory. To cope with the anticipated transport need, the TKO Study recommended the provision of Tseung Kwan O – Lam Tin Tunnel (TKO-LTT) (hereinafter referred to as “the Project”) and Cross Bay Link (CBL) to meet the long-term traffic demand between TKO and the external areas. The site layout plan for the Project is shown in **Figure 1**.
- 2.3 The Environmental Impact Assessment (EIA) Report for the TKO-LTT project was approved under the Environmental Impact Assessment Ordinance (EIAO) in July 2013. The corresponding Environmental Permit (EP) was issued in August 2013 (EP no.: EP-458/2013). Variations to the EP was applied and the latest EP (EP no.: EP-458/2013/C) was issued by the Director of Environmental Protection (DEP) in January 2017.
- 2.4 The commencement dates of construction of this Project is:
- Contract No. NE/2015/01 and Contract No. NE/2015/02: 7 November 2016.
 - Contract No. NE/2015/03: 29 May 2017.

Project Organizations

- 2.5 Different parties with different levels of involvement in the project organization include:
- Project Proponent – Civil Engineering and Development Department (CEDD)
 - The Engineer and the Engineer’s Representative (ER) – AECOM
 - Environmental Team (ET) – Cinotech Consultants Limited (Cinotech)
 - Independent Environmental Checker (IEC) – AnewR Consulting Limited (AnewR)
- 2.6 The key contacts of the Project are shown in **Table 2.1**.

Table 2.1 Key Project Contacts

| Party | Role | Contact Person | Phone No. | Fax No. |
|----------|-----------------------------------|--------------------------|-----------|-----------|
| CEDD | Project Proponent | Mr. Chiang Nin Tat, Eric | 2301 1384 | 2739 0076 |
| AECOM | Engineer’s Representative | Mr. KY Chan | 3922 9000 | 2759 1698 |
| Cinotech | Environmental Team | Dr. Priscilla Choy | 2151 2089 | 3107 1388 |
| | | Ms. Ivy Tam | 2151 2090 | |
| AnewR | Independent Environmental Checker | Mr. Adi Lee | 2618 2836 | 3007 8648 |

Construction Activities undertaken during the Reporting Month

2.7 The major site activities undertaken in the reporting month included:

Table 2.2 Summary Table for Major Site Activities in the Reporting Month

| Contract No. | Project Title | Site Activities (October 2017) | |
|---------------------|---|--|---|
| NE/2015/01 | Tseung Kwan O – Lam Tin Tunnel – Main Tunnel and Associated Works | Lam Tin Interchange | 1) EHC2 U-Trough 2) Site Formation – Area 1G1, Area 1G2, 2, 3, 4 & Area 5 3) Pipe Pile wall – Area 2A |
| | | Main Tunnel | 1) Main Tunnel Excavation |
| | | TKO Interchange | 1) Haul Road Construction and Site Formation & Slope Works 2) Temporary Cut Slope For BMCPC 3) Temporary Barging Facilities & Temporary Platform 4) Steel Platform for Bridge Construction |
| NE/2015/02 | Tseung Kwan O – Lam Tin Tunnel – Road P2 and Associated Works | 1) Site Clearance - Removal of vegetation and general refuse in Portion V and VI 2) Hoarding Erection 3) Advance Works for Construction of Steel Cofferdam in Portion VIII and Area Y 4) Reinstatement of Temporary Steel Cofferdam and Double Water Gate 5) Construction of Retaining Wall (Portion VIII and Area Y) 6) Re-provision of DSD transformation room (Portion I) 7) Piling works at Tong Yin Street (Portion VI) 8) Pre-bored works at Portion IV & VII 9) Demolition of Existing Transformer Room (Portion III) | |
| NE/2015/03 | Tseung Kwan O – Lam Tin Tunnel – Northern Footbridge | 1) Foundation piling at West Pier 2) Pile Cap Construction (with ELS) at East Pier 3) Pile Construction at East Pier | |

2.8 The construction programme showing the inter-relationship with environmental protection/mitigation measures are presented in **Table 2.3**.

Table 2.3 Construction Programme Showing the Inter-Relationship with Environmental Protection/Mitigation Measures

| Construction Works | Major Environmental Impact | Control Measures |
|---------------------------|--|--|
| As mentioned in Table 2.2 | Noise, dust impact, water quality and waste generation | <ul style="list-style-type: none"> • Sufficient watering of the works site with active dust emitting activities • Properly cover the stockpiles • On-site waste sorting and implementation of trip ticket system • Appropriate desilting/sedimentation devices provided on site for treatment before discharge • Use of quiet plant and well-maintained construction plant • Provide movable noise barrier |

Status of Environmental Licences, Notification and Permits

2.9 A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project is presented in Table 2.4.

Table 2.4 Summary of the Status of Environmental Licences, Notification and Permits

| Contract No. | Permit / License No. | Valid Period | | Status |
|--|--------------------------------------|--------------|------------|--------|
| | | From | To | |
| Environmental Permit (EP) | | | | |
| N/A | EP-458/2013/C | 20/1/2017 | N/A | Valid |
| Notification pursuant to Air Pollution Control (Construction Dust) Regulation | | | | |
| NE/2015/01 | EPD Ref no.: 405305 | 21/07/2016 | N/A | Valid |
| | EPD Ref no.: 405582 | 28/07/2016 | N/A | Valid |
| NE/2015/02 | EPD Ref no.: 406100 | 12/08/2016 | N/A | Valid |
| NE/2015/03 | EPD Ref no.: 416072 | 26/04/2017 | N/A | Valid |
| Billing Account for Construction Waste Disposal | | | | |
| NE/2015/01 | Account No. 7025431 | 11/07/2016 | N/A | Valid |
| NE/2015/02 | Account No. 7025654 | 16/08/2016 | N/A | Valid |
| NE/2015/03 | Account No. 7026805 | 30/12/2016 | N/A | Valid |
| Vessel Billing Account under construction waste disposal charging scheme | | | | |
| NE/2015/01 | Account No. 7027764 | 22/08/2017 | 10/11/2017 | Valid |
| Registration of Chemical Waste Producer | | | | |
| NE/2015/01 | Waste Producer No. 5218-290-L2881-02 | 22/08/2016 | N/A | Valid |
| | Waste Producer No. 5213-833-L2532-03 | 22/08/2016 | N/A | Valid |
| NE/2015/02 | Waste Producer No. 5213-838-C4094-01 | 23/08/2016 | N/A | Valid |
| NE/2015/03 | Waste Producer No. 5213-265-W3435-04 | 19/07/2017 | N/A | Valid |
| Effluent Discharge License under Water Pollution Control Ordinance | | | | |
| NE/2015/01 | WT00025806-2016 | 22/11/2016 | 30/11/2021 | Valid |

| Contract No. | Permit / License No. | Valid Period | | Status |
|--|----------------------|--------------|------------|----------------------------|
| | | From | To | |
| | WT00026212-2016 | 25/11/2016 | 30/11/2021 | Valid |
| | WT00027354-2017 | 22/03/2017 | 31/03/2022 | Valid |
| | WT00027405-2017 | 22/03/2017 | 31/03/2022 | Valid |
| | WT-00028495-2017 | 11/08/2017 | 31/08/2022 | Valid |
| NE/2015/02 | WT00026386-2016 | 15/12/2016 | 31/12/2021 | Valid |
| | WT00027226-2017 | 23/02/2017 | 28/02/2022 | Valid |
| NE/2015/03 | WT00027295-2017 | 20/03/2017 | 18/04/2019 | Valid |
| | WT00027266-2017 | 08/03/2017 | 18/04/2019 | Valid |
| Construction Noise Permit (CNP) | | | | |
| NE/2015/01 | GW-RE0508-17 | 27/06/2017 | 22/12/2017 | Valid |
| | GW-RE0699-17 | 05/09/2017 | 04/11/2017 | Valid |
| | GW-RE0721-17 | 08/09/2017 | 07/12/2017 | Valid |
| | GW-RE0760-17 | 23/09/2017 | 22/11/2017 | Valid |
| | GW-RE0705-17 | 06/09/2017 | 05/03/2018 | Valid |
| | GW-RE0656-17 | 27/08/2017 | 26/10/2017 | Expired on 26 October 2017 |
| | GW-RE0838-17 | 30/10/2017 | 29/12/2017 | Valid |
| | GW-RE0828-17 | 27/10/2017 | 26/01/2018 | Valid |
| | GW-RE0835-17 | 27/10/2017 | 26/12/2017 | Valid |
| NE/2015/02 | GW-RE0281-17 | 13/04/2017 | 02/10/2017 | Expired on 2 October 2017 |
| | GW-RE0414-17 | 02/06/2017 | 01/12/2017 | Valid |
| | GW-RE0516-17 | 29/06/2017 | 22/12/2017 | Valid |
| | GW-RE0670-17 | 29/08/2017 | 28/10/2017 | Expired on 28 October 2017 |
| | GW-RE0800-17 | 11/10/2017 | 10/04/2018 | Valid |
| | GW-RE0809-17 | 13/10/2017 | 12/04/2018 | Valid |
| | GW-RE0826-17 | 30/10/2017 | 29/01/2018 | Valid |
| Marine Dumping Permit | | | | |

| Contract No. | Permit / License No. | Valid Period | | Status |
|--------------|----------------------|--------------|------------|--------|
| | | From | To | |
| NE/2015/02 | EP/MD/18-014 | 15/06/2017 | 14/12/2017 | Valid |

Summary of EM&A Requirements

- 2.10 The EM&A programme requires construction noise monitoring, air quality monitoring, water quality monitoring, environmental site audit, etc. The EM&A requirements for each parameter are described in the following sections, including:
- All monitoring parameters;
 - Action and Limit levels for all environmental parameters;
 - Event Action Plans;
 - Environmental mitigation measures, as recommended in the Project EIA Report.
- 2.11 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 10 of this report.
- 2.12 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the monitoring parameters of the required environmental monitoring works and audit works for the Project in October 2017.

3. AIR QUALITY

Monitoring Requirements

- 3.1 According to EM&A Manual of the Project, 1-hour and 24-hour TSP monitoring are required to monitor the air quality. For regular impact monitoring, a sampling frequency of at least once in every six days shall be undertaken at all of the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six days shall be undertaken when the highest dust impact occurs. **Appendix A** shows the established Action/Limit Levels for the environmental monitoring works.

Monitoring Locations

- 3.2 Six designated monitoring stations were selected for air quality monitoring programme. **Table 3.1** describes the air quality monitoring locations, which are also depicted in **Figure 2**.

Table 3.1 Locations for Air Quality Monitoring

| Monitoring Stations | Location | Location of Measurement |
|---------------------------|--|-------------------------|
| AM1 | Tin Hau Temple | Ground Level |
| AM2 | Sai Tso Wan Recreation Ground | Ground Level |
| AM3 | Yau Lai Estate Bik Lai House | Rooftop (41/F) |
| AM4 ⁽¹⁾ | Sitting-out Area at Cha Kwo Ling Village | Ground Level |
| AM4(A) ^{(2) (*)} | Cha Kwo Ling Public Cargo Working Area Administrative Office | Rooftop (3/F) |
| AM5(A) ^(*) | Tseung Kwan O DSD Desilting Compound | Ground Level |
| AM6(A) ^(*) | Park Central, L1/F Open Space Area | 1/F |

Remarks: (1) For 1-hour TSP monitoring; (2) For 24-hour TSP monitoring

(*) Air quality monitoring at designated station AM4(24-hr TSP), AM5 and AM6 was rejected by the premise owners. Therefore, baseline and impact air quality monitoring works were carried out at alternative air quality monitoring stations AM4(A) (24-hr TSP only), AM5(A) and AM6(A) respectively.

Monitoring Equipment

- 3.3 High Volume Samplers (HVS) were used to carry out 24-hour TSP monitoring. Direct reading dust meter were also used to measure 1-hour average TSP levels. The 1-hour sampling was determined periodically by HVS to check the validity and accuracy of the results measured by direct reading method.
- 3.4 Wind data monitoring equipment was set at rooftop (about 41/F) of Yau Lai Estate Bik Lai House for logging wind speed and wind direction such that the wind sensors are clear of obstructions or turbulence caused by building. The wind data monitoring equipment is re-calibrated at least once every six months and the wind directions are divided into 16 sectors of 22.5 degrees each. The location is shown in **Figure 2**.
- 3.5 **Table 3.2** summarizes the equipment to be used in the air quality monitoring. Copies of calibration certificates are attached in **Appendix B**. Equipments was not used for monitoring in the period after “Next Due Date” stated in the respective calibration certificates.

Table 3.2 Air Quality Monitoring Equipment

| Equipment | Model and Make | Quantity |
|-----------------------|--|----------|
| Calibrator | TISCH Model: TE-5025A | 1 |
| 1-hour TSP Dust Meter | Sibata Model No.: LD-3 / LD-3B | 0 |
| | Met One Instruments Model No.: AEROCET-531 | 0 |
| | Handheld Particle Counter Hal-HPC300 / Hal-HPC301 | 6 |
| HVS Sampler | TISCH Model: TE-5170 | 1 |
| | GMW Model: GS2310 | 5 |
| Wind Anemometer | Davis Weather Monitor II, Model no. 7440 | 1 |

Monitoring Parameters and Frequency

3.6 **Table 3.3** summarizes the monitoring parameters, monitoring period and frequencies of air quality monitoring.

Table 3.3 Frequency and Parameters of Air Quality Monitoring

| Monitoring Stations | Parameter | Frequency |
|---|-------------|-------------------|
| AM1, AM2, AM3, AM4, AM5(A) and AM6(A) | 1-hour TSP | 3 times per 6 day |
| AM1, AM2, AM3, AM4(A), AM5(A) and AM6(A) | 24-hour TSP | Once per 6 days |

Monitoring Methodology***1-hour TSP Monitoring******Measuring Procedures***

3.7 The measuring procedures of the 1-hour dust meter are in accordance with the Manufacturer's Instruction Manual as follows:

(Model LD3 / LD3B)

- The 1-hour dust meter is placed at least 1.3 meters above ground.
- Set POWER to "ON" and make sure that the battery level was not flash or in low level.
- Allow the instrument to stand for about 3 minutes and then the cap of the air sampling inlet has been released.
- Push the knob at MEASURE position.
- Set time/mode setting to [BG] by pushing the time setting switch. Then, start the background measurement by pushing the start/stop switch once. It will take 6 sec. to complete the background measurement.
- Push the time setting switch to change the time setting display to [MANUAL] at the bottom left of the liquid crystal display. Finally, push the start/stop switch to stop the measuring after 1 hour sampling.
- Information such as sampling date, time, count value and site condition were recorded during the monitoring period.

(AEROCET-531)

- The 1-hour dust meter is placed at least 1.3 meters above ground.
 - Remove the red rubber cap from the AEROCET-531 inlet nozzle.
 - Turn on the power switch that is located on the right side of the AEROCET-531.
 - On power up the product intro screen is displayed for 3 seconds. The intro screen

displays the product name and firmware version.

- Then the main counter screen will be displayed.
- Press the START button. Internal vacuum pump start running. After 1 minute the pump will stop and the 0.5 μ m and 5 μ m channels will show the cumulative counts of particles larger than 0.5 μ m and 5 μ m per cubic foot.
- The AEROCET-531 is now checked out and ready for use.
- To switch off the AEROCET-531 power to stop the measuring after 1 hour sampling.
- Information such as sampling date, time, and display value and site condition were recorded during the monitoring period.

(Equipment: Hal Technology; Model no. Hal-HPC300)

- The 1-hour dust meter is placed at least 1.3 meters above ground.
- Set POWER to “ON” and make sure that the battery level was not flash or in low level.
- Allow the instrument to stand for about 3 minutes and then the cap of the air sampling inlet has been released.
- Push the knob at MEASURE position.
- Set time/mode setting to [BG] by pushing the time setting switch. Then, start the background measurement by pushing the start/stop switch once. It will take 6 sec. to complete the background measurement.
- Push the time setting switch to change the time setting display to [MANUAL] at the bottom left of the liquid crystal display. Finally, push the start/stop switch to stop the measuring after 1 hour sampling.
- Information such as sampling date, time, count value and site condition were recorded during the monitoring period.

Maintenance/Calibration

3.8 The following maintenance/calibration is required for the direct dust meters:

- Check and calibrate the meter by HVS to check the validity and accuracy of the results measured by direct reading method at 2-month intervals throughout all stages of the air quality monitoring.

24-hour TSP Monitoring

Instrumentation

3.9 High volume samplers (HVS) (TISCH Model: TE-5170) complete with appropriate sampling inlets were employed for 24-hour TSP monitoring. The sampler is composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complied with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

3.10 The positioning of the HVS samplers are as follows:

- a horizontal platform with appropriate support to secure the samplers against gusty wind shall be provided;
- no two samplers shall be placed less than 2 meter apart
- the distance between the sampler and an obstacle, such as buildings, must be at least twice the height that the obstacle protrudes above the sampler;
- a minimum of 2 metres of separation from walls, parapets and penthouses is required for rooftop samplers;
- a minimum of 2 metres of separation from any supporting structure, measured horizontally is required;

- no furnace or incinerator flue is nearby;
- airflow around the sampler is unrestricted;
- the sampler is more than 20 metres from the dripline;
- any wire fence and gate, to protect the sampler, shall not cause any obstruction during monitoring;
- permission must be obtained to set up the samplers and to obtain access to the monitoring stations; and
- a secured supply of electricity is needed to operate the samplers.

Operating/analytical procedures for the operation of HVS

- 3.11 Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 1.1 m³/min. and 1.4 m³/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50.
- 3.12 For TSP sampling, fiberglass filters with a collection efficiency of > 99% for particles of 0.3µm diameter were used.
- 3.13 The power supply was checked to ensure the sampler worked properly. On sampling, the sampler was operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air monitoring station.
- 3.14 The filter holding frame was then removed by loosening the four nuts and a weighted and conditioned filter was carefully centered with the stamped number upwards, on a supporting screen.
- 3.15 The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- 3.16 The shelter lid was closed and secured with the aluminum strip.
- 3.17 The timer was then programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).
- 3.18 After sampling, the filter was removed and sent to the HOKLAS laboratory (Wellab Ltd.) for weighing. The elapsed time will be also recorded.
- 3.19 Before weighing, all filters was equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than ±3°C; the relative humidity (RH) should be < 50% and not vary by more than ±5%. A convenient working RH is 40%.

Maintenance/Calibration

- 3.20 The following maintenance/calibration is required for the HVS:
- The high volume motors and their accessories will be properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking will be made to ensure that the equipment and necessary power supply are in good working condition.
 - High volume samplers will be calibrated at bi-monthly intervals using TE-5025A Calibration Kit throughout all stages of the air quality monitoring.

Results and Observations

- 3.21 All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 3.22 All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 3.23 The air temperature, precipitation and the relative humidity data was obtained from Hong Kong Observatory where the wind speed and wind direction were recorded by the installed Wind Anemometer at rooftop of Yau Lai Estate Bik Lai House (41/F). The location is shown in **Figure 2**. This weather information for the reporting month is summarized in **Appendix C**.
- 3.24 The monitoring data and graphical presentations of 1-hour and 24-hour TSP monitoring results are shown in **Appendix E** and **Appendix F** respectively.
- 3.25 The summary of exceedance record in reporting month is shown in **Appendix K**. No exceedance was recorded for the air quality monitoring.
- 3.26 According to our field observations, the major dust source identified at the designated air quality monitoring stations are as follows:

Table 3.4 Major Dust Source during Air Quality Monitoring

| Station | Major Dust Source |
|---|---|
| AM1 – Tin Hau Temple | Road Traffic at Cha Kwo Ling Road |
| AM2 – Sai Tso Wan Recreation Ground | N/A |
| AM3 – Yau Lai Estate Bik Lai House | Road Traffic near Eastern Cross Harbour Tunnel Toll Plaza |
| AM4 - Sitting-out Area at Cha Kwo Ling Village | Road Traffic at Cha Kwo Ling Road |
| AM4(A) - Cha Kwo Ling Public Cargo Working Area Administrative Office | Road Traffic at Cha Kwo Ling Road |
| AM5(A) - Tseung Kwan O DSD Desilting Compound | Vehicle Movement within the Desilting Compound |
| AM6(A) - Park Central, L1/F Open Space Area | Road Traffic at Po Yap Road |

4. NOISE

Monitoring Requirements

- 4.1 According to EM&A Manual of the Project, construction noise monitoring was conducted to monitor the construction noise arising from the construction activities. The regular monitoring frequency for each monitoring station shall be on a weekly basis and conduct one set of measurements between 0700 and 1900 hours on normal weekdays. **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.

Monitoring Locations

- 4.2 Noise monitoring was conducted at 8 designated monitoring stations (CM1, CM2, CM3, CM4, CM5, CM6(A), CM7(A), CM8(A)) in the reporting period. **Table 4.1** and **Figure 3** show the locations of these stations.

Table 4.1 Noise Monitoring Stations

| Monitoring Stations | Locations | Location of Measurement |
|---------------------|---|-------------------------|
| CM1 | Nga Lai House, Yau Lai Estate Phase 1, Yau Tong | Rooftop (41/F) |
| CM2 | Bik Lai House, Yau Lai Estate Phase 1, Yau Tong | Rooftop (41/F) |
| CM3 | Block S, Yau Lai Estate Phase 5, Yau Tong | Rooftop (40/F) |
| CM4 | Tin Hau Temple, Cha Kwo Ling | Ground Level |
| CM5 | CCC Kei Faat Primary School, Yau Tong | Rooftop (6/F) |
| CM6(A)* | Site Boundary of Contract No. NE/2015/02 near Tower 1, Ocean Shores | Ground Level |
| CM7(A)* | Site Boundary of Contract No. NE/2015/02 near Tower 7, Ocean Shores | Ground Level |
| CM8(A)* | Park Central, L1/F Open Space Area | 1/F |

Remarks: * Noise monitoring at designated station CM6, CM7 & CM8 was rejected by the premise owners. Therefore, baseline and impact noise monitoring works were carried out at alternative noise monitoring stations CM6(A), CM7(A) and CM8(A) respectively.

Monitoring Equipments

- 4.3 Integrating Sound Level Meter was used for impact noise monitoring. The meters are Type 1 sound level meter capable of giving a continuous readout of the noise level readings including equivalent continuous sound pressure level (L_{eq}) and percentile sound pressure level (L_x) that also complied with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications. **Table 4.2** summarizes the noise monitoring equipment being used. Copies of calibration certificates are attached in **Appendix B**. Equipments was not used for monitoring in the period after “Next Due Date” stated in the respective calibration certificates.

Table 4.2 Noise Monitoring Equipment

| Equipment | Model and Make | Quantity |
|-------------------------------|-------------------|----------|
| Integrating Sound Level Meter | SVAN 955 / 957 | 6 |
| | BSWA 801 | 0 |
| Calibrator | SV30A | 3 |
| | Brüel & Kjær 4231 | 2 |

- 4.4 **Table 4.3** summarizes the monitoring parameters, frequency and total duration of monitoring. The noise monitoring schedule is shown in **Appendix D**.

Table 4.3 Frequency and Parameters of Noise Monitoring

| Monitoring Stations | Parameter | Period | Frequency | Measurement |
|---------------------|---|-------------------------------------|------------------|-------------|
| CM1 | L ₁₀ (30 min) dB(A) L ₉₀ (30 min) dB(A) L _{eq} (30 min) dB(A) | 0700-1900 hrs on normal weekdays | Once per week | Façade |
| CM2 | | | | Façade |
| CM3 | | | | Façade |
| CM4 | | | | Façade |
| CM5 | | | | Façade |
| CM6(A) | | | | Free Field |
| CM7(A) | | | | Free Field |
| CM8(A) | | | | Façade |

Monitoring Methodology and QA/QC Procedure

- 4.5 The monitoring procedures are as follows:
- The monitoring station was normally be at a point 1m from the exterior of the sensitive receivers building façade and be at a position 1.2m above the ground.
 - For free field measurement, the meter was positioned away from any nearby reflective surfaces. All records for free field noise levels was adjusted with a correction of +3 dB(A).
 - The battery condition was checked to ensure the correct functioning of the meter.
 - Parameters such as frequency weighting, the time weighting and the measurement time was set as follows:
 - frequency weighting : A
 - time weighting : Fast
 - measurement time : 30 minutes
 - Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement will be more than 1.0 dB, the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.
 - At the end of the monitoring period, the L_{eq}, L₉₀ and L₁₀ was recorded. In addition, noise sources was recorded on a standard record sheet.
 - Noise monitoring will be cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s. Supplementary monitoring was provided to ensure sufficient data would be obtained.

Maintenance and Calibration

- 4.6 The microphone head of the sound level meter and calibrator was cleaned with a soft cloth at quarterly intervals.
- 4.7 The sound level meter and calibrator was checked and calibrated at yearly intervals.
- 4.8 Immediately prior to and following each noise measurement the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration levels from before and after the noise measurement agree to within 1.0 dB.

Results and Observations

- 4.9 All noise monitoring was conducted as scheduled in the reporting month. Five Action Level exceedance was recorded due to the documented complaints received. One Limit Level exceedance was recorded in the reporting month. The summary of exceedance record in the reporting month is shown in **Appendix K**.
- 4.10 Noise monitoring results and graphical presentations are shown in **Appendix G**.
- 4.11 The major noise source identified at the noise monitoring stations are shown in **Table 4.4**.

Table 4.4 Major Noise Source during Noise Monitoring

| Monitoring Stations | Locations | Major Noise Source |
|---------------------|---|---|
| CM1 | Nga Lai House, Yau Lai Estate Phase 1, Yau Tong | Road Traffic near Eastern Cross Harbour Tunnel Toll Plaza |
| CM2 | Bik Lai House, Yau Lai Estate Phase 1, Yau Tong | Road Traffic near Eastern Cross Harbour Tunnel Toll Plaza |
| CM3 | Block S, Yau Lai Estate Phase 5, Yau Tong | Road Traffic near Eastern Cross Harbour Tunnel Toll Plaza |
| CM4 | Tin Hau Temple, Cha Kwo Ling | Road Traffic at Cha Kwo Ling Road |
| CM5 | CCC Kei Faat Primary School, Yau Tong | Road Traffic at Yau Tong Road |
| CM6(A) | Site Boundary of Contract No. NE/2015/02 near Tower 1, Ocean Shores | Road Traffic at O King Road near Ocean Shores |
| CM7(A) | Site Boundary of Contract No. NE/2015/02 near Tower 7, Ocean Shores | Road Traffic at Tong Yin Street |
| CM8(A) | Park Central, L1/F Open Space Area | Road Traffic at Po Yap Road |

- 4.12 All the Construction Noise Levels (CNLs) reported in this report were adjusted with the corresponding baseline level (i.e. Measured L_{eq} – Baseline L_{eq} = CNL), in order to facilitate the interpretation of the noise exceedance. The baseline noise level and the Noise Limit Level at each designated noise monitoring station are presented in **Table 4.5**.

Table 4.5 Baseline Noise Level and Noise Limit Level for Monitoring Stations

| Station | Baseline Noise Level, dB (A) (at 0700 – 1900 hrs on normal weekdays) | Noise Limit Level, dB (A) (at 0700 – 1900 hrs on normal weekdays) |
|---------|---|--|
| CM1 | 65.5 | 75 |
| CM2 | 63.6 | |
| CM3 | 65.6 | |
| CM4 | 62.0 | |
| CM5 | 68.2 | 70* |
| CM6(A) | 61.9 | 75 |
| CM7(A) | 58.3 | |
| CM8(A) | 69.1 | |

(*) Noise Limit Level is 65 dB(A) during school examination periods.

Updated Construction Noise Assessment

Contract No. NE/2015/01, Contract No. NE/2015/02 and Contract No. NE/2015/03

- 4.13 No update of Construction Noise Assessment in the reporting period. Any updated Construction Noise Assessment will be shown in **Appendix S**.

5. WATER QUALITY

Monitoring Requirements

Groundwater Quality

- 5.1 Groundwater quality monitoring shall be conducted as identified in the EIA report (locations refer to **Figure 4**, Stream 1 to 3). According to the EM&A Manual, dissolved oxygen (DO), pH, temperature, turbidity, suspended solids (SS), 5-day biochemical oxygen demand (BOD₅), Total organic carbon (TOC), Total Nitrogen, Ammonia-N and Total Phosphate are the parameters for the monitoring. **Appendix A** shows the established Action and Limit Levels.
- 5.2 As stated in the Baseline Environmental Monitoring Plan submitted to EPD in September 2016, Groundwater quality monitoring could not be conducted at the other identified monitoring station in the EIA Report, Stream 4, as it was found to be not accessible due to safety reason. EPD has no further comment on the Plan in October 2016.

Marine Water Quality

- 5.3 Marine water quality monitoring was conducted three times per week at the designated monitoring stations. Monitoring took place two times per monitoring day during mid ebb and mid flood tides at three depths (1 meter from surface, mid depth and 1 meter from the bottom). For Tseung Kwan O Salt Water Intake (i.e. Station M6), water sampling and in situ measurements was taken at the vertical level where the water abstraction point of the intake is located (i.e. approximately mid-depth level). If the water depth is less than 6m, the mid-depth measurement may be omitted. If the depth is less than 3m, only the mid-depth measurements need to be taken.
- 5.4 Duplicate in-situ measurements (Dissolved oxygen (DO) concentration, DO saturation, turbidity, pH, temperature and salinity) and water samples (suspended solids (SS)) at each depth were monitored in accordance with the requirements in the EM&A Manual. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides were not less than 0.5m.

Groundwater Level Monitoring (Piezometer Monitoring)

- 5.5 Daily piezometer monitoring at any time of the day shall be carried throughout the whole period when any tunnel construction activities are carried out within +/- 50m of the piezometer gate in plan. The monitoring has not commenced in this reporting period.

Monitoring Locations

Groundwater Quality

- 5.6 Stream 1 – Stream 3 is designated for the groundwater quality monitoring according to EM&A Manual. The locations are also summarized in **Table 5.1** and shown on **Figure 4**.

Table 5.1 Groundwater Quality Monitoring Stations

| Monitoring Streams | Descriptions | Sampling Location |
|--------------------|--|-------------------------------------|
| Stream 1 | Stream running between the Kwong Tin Estate and Lei Yue Mun Road | 1 sampling location for each stream |
| Stream 2 | Stream on western coast of Chiu Keng Wan | |
| Stream 3 | Stream on western coast of Chiu Keng Wan | |

Marine Water Quality

- 5.7 A total of twelve monitoring stations are designated for the water quality monitoring program according to EM&A Manual. The locations are also summarized in **Table 5.2** and shown on **Figure 5**.

Table 5.2 Marine Water Quality Monitoring Stations

| Monitoring Stations | Descriptions | Coordinates | |
|---------------------|---|-------------|----------|
| | | Easting | Northing |
| M1 | Junk Bay Coral Site – Junk Bay near Chiu Keng Wan | 844255 | 817565 |
| M2 | Junk Bay Coral Site – Junk Bay | 844076 | 817087 |
| M3 | Junk Bay Coral Site – Junk Island | 844491 | 817890 |
| M4 | Junk Bay Coral Site – Chiu Keng Wan | 843209 | 816416 |
| M5 | Junk Bay Coral Site – Fat Tong Chau | 845463 | 815769 |
| M6 | Tseung Kwan O Salt Water Intake | 845512 | 817442 |
| C1 | Control Station – Southeast | 844696 | 814773 |
| C2 | Control Station – Northwest | 842873 | 816014 |
| G1 | Gradient Station | 844418 | 817560 |
| G2 | Gradient Station | 844290 | 817384 |
| G3 | Gradient Station | 844488 | 817735 |
| G4 | Gradient Station | 844967 | 817551 |

Monitoring Equipments

- 5.8 For in-situ monitoring, a multi-parameter meter (Aquaread AP-2000-D) was used to measure Dissolved oxygen (DO) concentration, DO saturation (DO %), pH, temperature and turbidity. A sampler was used to collect water samples for laboratory analysis of SS, BOD₅, TOC, Total Nitrogen, Ammonia-N and Total Phosphate.

Dissolved Oxygen (DO) and Temperature Measuring Equipment

- 5.9 The instrument for measuring dissolved oxygen and temperature was portable and weatherproof complete with cable, sensor, comprehensive operation manuals and use DC power source. It was capable of measuring:
- a dissolved oxygen level in the range of 0-20 mg/L and 0-200% saturation; and
 - a temperature of 0-45 degree Celsius.
- 5.10 It has a membrane electrode with automatic temperature compensation complete with a cable.
- 5.11 Sufficient stocks of spare electrodes and cables were available for replacement where necessary.
- 5.12 Salinity compensation was built-in in the DO equipment.

Turbidity

- 5.13 Turbidity was measured in situ by the nephelometric method. The instrument was portable and weatherproof using a DC power source complete with cable, sensor and comprehensive operation manuals. The equipment was capable of measuring turbidity between 0-1000 NTU. The probe cable was not be less than 25m in length.

pH

- 5.14 The instrument was consisting of a potentiometer, a glass electrode, a reference electrode and a temperature-compensating device. It was readable to 0.1pH in a range of 0 to 14. Standard buffer solutions of at least pH 7 and pH 10 were used for calibration of the instrument before and after use.

Water Depth Detector

- 5.15 A portable, battery-operated echo sounder was used for the determination of water depth at each designated monitoring station.

Water Sampler

- 5.16 Water samples collected for laboratory analysis were stored in high density polythene bottles sample containers, with appropriate preservatives added. All sampling bottles were labeled (waterproof) with the sampling date and time, sample lot number and sampling location reference number to avoid mishandling.

Sample Container and Storage

- 5.17 Following collection, water samples for laboratory analysis were stored in high density polythene bottles, with preservative appropriately added where necessary. They will be packed in ice (cooled to 4°C without being frozen), delivered to the laboratory and analysed as soon as possible.

Calibration of In Situ Instruments

- 5.18 All in situ monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or other international accreditation scheme before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the water quality monitoring.
- 5.19 For the on-site calibration of field equipment, the BS 1427:1993, "Guide to Field and on-site test methods for the analysis of waters" was observed.
- 5.20 Before each round of monitoring, a zero check in distilled water was performed with the turbidity probe of Aquaread AP-2000-D. The probe was then be calibrated with a solution of known NTU.
- 5.21 Sufficient stocks of spare parts were maintained for replacements when necessary. Backup monitoring equipment was also being made available so that monitoring can proceed uninterrupted even when some equipment is under maintenance, calibration, etc.
- 5.22 **Table 5.3** summarizes the equipment used in the water quality monitoring program. Copies of the calibration certificates of the equipment are shown in **Appendix B**. Equipments was not used for monitoring in the period after "Next Due Date" stated in the respective calibration certificates.

Table 5.3 Water Quality Monitoring Equipment

| Equipment | Model and Make | Qty. |
|--------------------------------------|---------------------------------------|------|
| Water Sampler | Kahlsico Water-Bottle Model 135DW 150 | 1 |
| Multi-parameter Water Quality System | YSI 6820-C-M | 0 |
| | Aquaread AP-2000-D | 0 |
| | YSI EXO1 Multiparameter Sondes | 4 |
| Monitoring Position Equipment | “Magellan” Handheld GPS Model GPS-320 | 1 |
| Water Depth Detector | Fishfinder 140 | 1 |

Monitoring Parameters and Frequency

5.23 **Table 5.4** summarizes the monitoring parameters, monitoring period and frequencies of the water quality monitoring in the reporting period.

Table 5.4 Water Quality Monitoring Parameters and Frequency

| Monitoring Stations | Parameters, unit | Depth | Frequency |
|--|---|---|--|
| Groundwater Quality | | | |
| Stream 1- Stream 3 | <ul style="list-style-type: none"> • DO, mg/L • DO Saturation, % • pH • Water Temperature (°C) • Turbidity, NTU • SS, mg/L • BOD₅, mg O₂/L • TOC, mg-TOC/L • Total Nitrogen, mg/L • Ammonia-N, mg NH₃-N/L • Total Phosphate, mg-P/L | Mid-depth | Biweekly (When the tunnel construction works are found within 50m of the location, weekly.) |
| Marine Water Quality | | | |
| M1 M2 M3 M4 M5 M6 C1 C2 G1 G2 G3 G4 | <p><i>In-situ:</i> Dissolved oxygen (DO) concentration, DO saturation, turbidity, pH, temperature and salinity</p> <p><u>Laboratory Testing:</u> Suspended Solids (SS)</p> | <p><u>M1-M5, C1-C2, G1-G4</u></p> <ul style="list-style-type: none"> • 3 water depths: 1m below water surface, mid-depth and 1m above sea bed. • If the water depth is less than 3m, mid-depth sampling only. • If the water depth is less than 6m, omit mid-depth sampling. <p><u>M6</u></p> <ul style="list-style-type: none"> • at the vertical level where the water abstraction point of the intake is located(i.e. approximately mid-depth level) | 3 days per week / 2 per monitoring day (1 for mid-ebb and 1 for mid-flood) |

Monitoring MethodologyGroundwater Quality

5.24 At each monitoring location, two consecutive in-situ measurements for DO concentration, DO saturation, pH, temperature and turbidity were taken for water samples on site. The probes were retrieved out of the water after the first measurement

and then re-deployed for the second measurement. Where the difference in the value between the first and second readings of each set was more than 25% of the value of the first reading, the reading was discarded and further readings were taken.

- 5.25 For SS, BOD₅, TOC, Total Nitrogen, Ammonia-N and Total Phosphate, measurement and grab samples of surface water was collected. Water samples of about adequate volume was collected and stored in high density polythene bottles. Following collection, water samples was stored in high density polythene bottles. Preservation H₂SO₄ was appropriately added for water samples for TOC, Total Nitrogen, Ammonia-N and Total Phosphate testing. Water samples was packed in ice and cooled to 4°C (without being frozen), delivered to the HOKLAS accredited laboratory, Wellab Limited and analyzed.

Marine Water Quality

- 5.26 The monitoring stations were accessed using survey boat by the guide of a hand-held Global Positioning System (GPS). The depth of the monitoring location was measured using depth meter in order to determine the sampling depths. Afterwards, the probes of the in-situ measurement equipment was lowered to the predetermined depths (1 m below water surface, mid-depth and 1 m above seabed) and the measurements was carried out accordingly. The in-situ measurements at predetermined depths was carried out in duplicate. In case the difference in the duplicate in-situ measurement results was larger than 25%, the third set of in-situ measurement would be carried out for result confirmation purpose.
- 5.27 Water sampler was lowered into the water to the required depths of sampling. Upon reaching the pre-determined depth, a messenger to activate the sampler was then released to travel down the wire. The water sample was sealed within the sampler before retrieving. At each station, water samples for SS at three depths (1 m below water surface, mid-depth and 1 m above seabed) were collected accordingly. Water samples were stored in a cool box and kept at less than 4°C but without frozen and sent to the laboratory as soon as possible.

Laboratory Analytical Methods

- 5.28 The testing of all parameters were conducted by Wellab Ltd. (HOKLAS Registration No.083) and comprehensive quality assurance and control procedures in place in order to ensure quality and consistency in results. The testing method and limit of reporting are provided in **Table 5.5**.

Table 5.5 Methods for Laboratory Analysis for Water Samples

| Parameters (Unit) | Proposed Method | Reporting Limit | Detection Limit |
|--|---|----------------------------------|-----------------|
| SS (mg/L) | APHA 2540 D | 0.5 mg/L ⁽¹⁾ | 0.5 mg/L |
| BOD ₅ (mg O ₂ /L) | APHA 19ed 5210B | 2 mg O ₂ /L | -- |
| TOC (mg-TOC/L) | In-house method SOP020 (Wet Oxidation) | 1 mg-TOC/L | -- |
| Total Nitrogen (mg/L) | In-house method SOP063 (FIA) | 0.6 mg/L | -- |
| Ammonia-N (mg NH ₃ -N/L) | In-house method SOP057 (FIA) | 0.05 mg NH ₃ - N/L | -- |
| Total Phosphorus (mg-P/L) ⁽²⁾ | In-house method SOP055 (FIA) | 0.05 mg-P/L | -- |

Note:

1) Limit of Reporting is reported as Detection Limit for non-HOKLAS report.

2) Parameter Total Phosphorus represents the laboratory testing for total phosphate content in water which is the sum of all three forms of phosphates in water.

QA/QC Requirements

Decontamination Procedures

- 5.29 Water sampling equipment used during the course of the monitoring programme was decontaminated by manual washing and rinsed clean seawater/distilled water after each sampling event. All disposal equipment was discarded after sampling.

Sampling Management and Supervision

- 5.30 Water samples were dispatched to the testing laboratory for analysis as soon as possible after the sampling. All samples were stored in a cool box and kept at less than 4°C but without frozen. All water samples were handled under chain of custody protocols and relinquished to the laboratory representatives at locations specified by the laboratory.
- 5.31 QA/QC procedures as attached in **Appendix J** are available for the parameters analyzed in the HOKLAS-accredited laboratory, WELLAB Ltd.

Results and Observations

Groundwater Quality Monitoring

- 5.32 All groundwater quality monitoring was conducted as scheduled in the reporting month. Summary of groundwater quality monitoring results is shown in **Table 5.6**. Groundwater monitoring results, graphical presentations and laboratory testing reports are shown in **Appendix H**.
- 5.33 Other relevant data was also recorded, such as monitoring location / position, time, sampling depth, weather conditions and any special phenomena or work underway nearby.
- 5.34 Action and Limit Level for groundwater monitoring has been reviewed with consideration of monitoring results obtained from November 2016 to June 2017, as there was no tunnel boring or tunnel construction works from November 2016 to June 2017. The updated Action and Limit Level is shown in **Appendix A**.

Table 5.6 Summary of Groundwater Quality Monitoring Results

| Date | Location | Parameters (unit) | | | | | | | | |
|-------------------|--------------|-------------------|-------------------------|-----------------|-----------|---|----------------|-----------------------|--|---------------------------|
| | | pH | Dissolved Oxygen (mg/L) | Turbidity (NTU) | SS (mg/L) | BOD ₅ (mg O ₂ /L) | TOC (mg-TOC/L) | Total Nitrogen (mg/L) | NH ₃ -N (mg NH ₃ -N/L) | Total Phosphorus (mg-P/L) |
| 12 October 2017 | Stream 1 | 7.9 | 7.8 | 2.0 | 0.5 | <2 | 3 | 1.4 | <0.05 | <0.05 |
| | Stream 2 | 7.9 | 7.7 | 1.9 | 10 | <2 | 3 | 1.6 | 0.06 | <0.05 |
| | Stream 3 | 8.0 | 7.8 | 0.8 | 0.8 | <2 | 2 | 1.4 | 0.11 | <0.05 |
| 26 October 2017 | Stream 1 | 7.6 | 7.8 | 1.4 | 1.0 | <2 | 3 | 0.6 | <0.05 | <0.05 |
| | Stream 2 | 7.6 | 7.8 | 1.4 | 1.4 | <2 | 3 | <0.6 | <0.05 | <0.05 |
| | Stream 3 | 7.6 | 7.8 | 1.3 | 0.8 | <2 | 3 | <0.6 | <0.05 | <0.05 |
| No. of Exceedance | Action Level | 0 | 0 | 0 | 1 | 0 | 0 | 0 | 0 | 0 |
| | Limit Level | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |

Note: ***Bold Italic*** means Action Level exceedance

Bold Italic with underline means Limit Level exceedance

5.35 Under the updated Action and Limit Level, three Action or Limit exceedances (shown below) are recorded in the period from July to October 2017.

| Date | Monitoring Location | Monitoring Parameter | Monitoring Results | Action Level | Limit Level |
|--------------|---------------------|----------------------|------------------------------|--------------|-------------|
| 18 July 2017 | Stream 3 | Suspended Solids | 10 mg/L | 7.6 | 12.1 |
| 28 Sep 2017 | Stream 1 | Ammonia-N | 0.24 mg NH ₃ -N/L | 0.15 | 0.20 |
| 12 Oct 2017 | Stream 2 | Suspended Solids | 10 mg/L | 7.6 | 12.1 |

5.36 It is considered that these exceedances are not project-related as there was no tunnel boring or tunnel construction works in Tseung Kwan O side from July to October 2017.

Marine Water Quality Monitoring

5.37 All marine water quality monitoring was conducted as scheduled in the reporting month. Marine water monitoring results and graphical presentations are shown in **Appendix I**. Other relevant data was also recorded, such as monitoring location / position, time, sampling depth, weather conditions and any special phenomena or work underway nearby.

5.38 Calculated Action and Limit Levels for Marine Water Quality is presented in **Appendix I**. No Action/Limit Level exceedance was recorded in the reporting period.

Groundwater Level Monitoring (Piezometer Monitoring)

5.39 Daily piezometer monitoring at any time of the day shall be carried throughout the whole period when any tunnel construction activities are carried out within +/- 50m of the piezometer gate in plan.

5.40 Construction Phase Piezometer Monitoring has not commenced in this reporting period.

6. ECOLOGY

Post-Translocation Coral Monitoring

- 6.1 Post-translocation monitoring survey is recommended in the EM&A Manual to audit the success of coral translocation. Information gathered during each post-translocation monitoring survey should include observations on the presence, survival, health condition and growth of the translocated coral colonies. These parameters should then be compared with the baseline results collected from the pre-translocation survey.
- 6.2 Under Contract No. NE/2015/01 and NE/2015/02, a total of 14 and 29 coral colonies were tagged and translocated respectively from the Donor Site to the Recipient Site in November 2016. Ten (10) corals at the Recipient Site were also tagged by each Contract as reference for post-translocation monitoring.
- 6.3 The post-translocation coral monitoring shall be conducted once every 3 months after completion for a period of 12 months. The third post-translocation coral monitoring was carried out on 22 August 2017.
- 6.4 The fourth post-translocation coral monitoring is scheduled to be carried out in November 2017 tentatively. Location of post-translocation coral monitoring is shown in **Figure 7**.

Event and Action Plan

- 6.5 The post-translocation monitoring result was evaluated against Action and Limit Levels presented in **Appendix A**. Evaluation was based on recorded changes in percentage of partial mortality of the corals.
- 6.6 If the defined Action Level or Limit Level for coral monitoring is exceeded, the actions as set out in **Appendix M** will be implemented.
- 6.7 If observations of any die-off / abnormal conditions of the translocated corals are made during the post-translocation monitoring, the ET shall inform the Contractor, IEC and AFCD, and liaise with AFCD to investigate any mitigation measures needed.

Results and Observations

- 6.8 No post-translocation coral monitoring was conducted in the reporting month.
- 6.9 Photographs of the coral colonies of coming post-translocation coral monitoring will be shown in **Appendix T**.

7. CULTURAL HERITAGE

Monitoring Requirement

- 7.1 According to the EP Conditions and EM&A Manual, monitoring of vibration impacts was conducted when the construction works are less than 100m from the Built Heritage in close proximity of the worksite, namely the Cha Kwo Ling Tin Hau temple. Tilting and settlement monitoring should be applied on the Cha Kwo Ling Tin Hau Temple. Construction works less than 100m from the Cha Kwo Ling Tin Hau temple commenced on 8 April 2017.
- 7.2 As stated in the approved “*Built Heritage Mitigation Plan*” for this Project, during the period of the construction works conducted within 100m from the Cha Kwo Ling Tin Hau Temple, monitoring on settlement and tilting will be conducted once a day for the Cha Kwo Ling. Monitoring of vibration will be conducted during blasting at Cha Kwo Ling area once a day. When there is no blasting to be conducted at the area, vibration monitoring at the Cha Kwo Ling Tin Hau Temple will be conducted once per day when there are piling works or rock breaking works within the 100m from the Cha Kwo Ling Tin Hau Temple.

Monitoring Locations

- 7.3 One (1) vibration monitoring point, one (1) building settlement monitoring point and one (1) building tilting monitoring point are proposed for the vibration impacts monitoring of the construction works. The building settlement marker and the tiltmeter will be placed on the wall of the Cha Kwo Ling Tin Hau Temple and the vibration monitoring point is located within the Cha Kwo Ling Tin Hau Temple.
- 7.4 Confirmation from the Cha Kwo Ling Tin Hau Temple on the installation of these monitoring equipment is yet to be obtained by the Contractor. Vibration monitoring was carried out at a temporary location outside the Cha Kwo Ling Tin Hau Temple in the reporting period. Monitoring Location is shown in **Figure 8**.

Monitoring Equipment

- 7.5 Building settlement was measured by surveyors via settlement marker and tiltmeter attached to the wall of the Cha Kwo Ling Tin Hau Temple.
- 7.6 Vibration monitoring was conducted by using vibrographs: Minimate Plus manufactured by InstanTel. These vibrographs will be calibrated annually and its performance follows the requirements given in the “*Guidance Note on Vibration Monitoring*” (GN-VM) issued by the Civil Engineering and Development Department, which is based on the Performance Specification for Blasting Seismographs by International Society of Explosive Engineers (ISEE (2000)).
- 7.7 **Table 7.1** summarizes the equipment employed by the Contractor for vibration monitoring. Copies of calibration certificates are attached in **Appendix B**.

Table 7.1 Vibration Monitoring Equipment

| Equipment | Manufacturer and Model | Quantity |
|---|--|----------|
| DNA03 Digital Level for building settlement and tilting | Leica Geosystems Article No.: 723289 | 1 |
| Vibrographs for vibration monitoring | MiniMate Plus manufactured by InstanTel Model No.: 716A0403 | 2 |

Monitoring Methodology

- 7.8 Vibrograph (velocity seismograph) was deployed at each monitoring station to measure and record the PPV and amplitude of ground motion in three mutually perpendicular directions. Vibration monitoring equipment fulfils the requirements stated in the Government guidelines and is calibrated to HOKLAS standards. Each monitoring would not be more than 10 minutes. Settlement and tilting monitoring should be conducted by surveyors manually.

Alert, Alarm and Action Levels

- 7.9 The Alert, Alarm and Action (AAA) Levels are given in **Table 7.2**.

Table 7.2 AAA Levels for Monitoring for Cultural Heritage

| Parameter | Alert Level | Alarm Level | Action Level |
|-----------------------------|---------------|---------------|---|
| Vibration | ppv: 4.5 mm/s | ppv: 4.8 mm/s | ppv: 5mm/s Maximum Allowable Vibration Amplitude: 0.1mm |
| Building Settlement Markers | 6mm | 8mm | 10mm |
| Building Tilting | 1:2000 | 1:1500 | 1:1000 |

Results

- 7.10 In the reporting month, vibration monitoring was carried out by the Contractor at the aforesaid location on 23 occasions. No AAA Level exceedance for vibration monitoring was recorded in the reporting month. The monitoring results are provided in **Table 7.3**.

Table 7.3 Vibration Monitoring Results

| Date | Time | Tilting | Settlement (mm) | Vibration (mm/s) | | |
|-----------|-------|---------|-----------------|-----------------------|----------|--------------|
| | | | | Measurement Direction | | |
| | | | | Tran | Vertical | Longitudinal |
| 03-Oct-17 | 17:35 | -1 | 0 | 0.254 | 0.127 | 0.127 |
| 04-Oct-17 | 16:09 | -2 | +1 | 0.254 | 0.127 | 0.127 |
| 06-Oct-17 | 14:25 | -1 | +1 | 0.254 | 0.127 | 0.127 |
| 07-Oct-17 | 13:19 | -1 | +1 | 0.254 | 0.254 | 0.127 |
| 09-Oct-17 | 14:35 | -2 | 0 | 0.127 | 0.381 | 0.127 |
| 10-Oct-17 | 16:30 | -2 | +1 | 0.127 | 0.127 | 0.127 |
| 11-Oct-17 | 10:06 | -3 | 0 | 0.254 | 0.127 | 0.127 |
| 12-Oct-17 | 8:42 | -1 | +1 | 0.127 | 0.127 | 0.127 |
| 13-Oct-17 | 10:22 | -2 | 0 | 0.127 | 0.127 | 0.127 |
| 14-Oct-17 | 17:13 | -3 | 0 | Technical Error | | |
| 16-Oct-17 | 16:44 | 0 | 0 | 0.127 | 0.127 | 0.127 |
| 17-Oct-17 | 14:11 | -1 | 0 | 0.254 | 0.127 | 0.127 |
| 18-Oct-17 | 9:44 | 0 | +2 | 0.127 | 0.254 | 0.127 |
| 19-Oct-17 | 10:05 | 0 | +2 | 0.254 | 0.381 | 0.127 |
| 20-Oct-17 | 16:32 | -1 | 0 | 0.254 | 0.127 | 0.127 |
| 21-Oct-17 | 17:04 | -1 | +1 | 0.254 | 0.254 | 0.254 |
| 23-Oct-17 | 14:28 | 0 | +2 | 0.127 | 0.127 | 0.127 |
| 24-Oct-17 | 13:58 | -2 | 0 | 0.127 | 0.127 | 0.127 |
| 25-Oct-17 | 15:08 | -2 | +1 | 0.127 | 0.127 | 0.127 |
| 26-Oct-17 | 10:37 | -1 | +1 | 0.127 | 0.127 | 0.127 |
| 27-Oct-17 | 11:07 | -2 | +2 | 0.254 | 0.254 | 0.127 |
| 30-Oct-17 | 13:59 | -1 | +1 | 0.254 | 0.127 | 0.127 |
| 31-Oct-17 | 16:09 | -1 | +1 | 0.127 | 0.127 | 0.127 |

Mitigation Measures for Cultural Heritage

- 7.11 According to Condition 3.6 of the EP (EP No.: EP-458/2013/C), to prevent damage to Cha Kwo Ling Tin Hau Temple and its Fung Shui rocks (Child-given rocks) during the construction phase, a temporarily fenced-off buffer zone (Rocks buffer zone is 5 m from the edge of Rocks and 15m from the edge of Rocks alter) with allowance for public access (minimum 1 m) around the temple and the Fung Shui rocks shall be provided. The open yard in front of the temple should be kept as usual for annual Tin Hau festival.
- 7.12 As there is a large buffer distance from the current works to Cha Kwo Ling Tin Hau Temple and the Fung Shui rocks (Child-given rocks), the temporarily fenced-off rocks buffer zone and from the edge of Rocks alter is not required. The fenced-off rocks buffer zone would be implemented when there is construction activities in vicinity of the cultural heritage.

8. LANDSCAPE AND VISUAL IMPACT REQUIREMENTS

- 8.1 Landscape and visual mitigation measures during the construction phase shall be checked to ensure that they are fully realized and implemented on site.
- 8.2 Site audits were carried out on a weekly basis to monitor and audit the timely implementation of landscape and visual mitigation measures. The summaries of site audits are attached in **Appendix L**.
- 8.3 No non-compliance of the landscape and visual impact was recorded in the reporting month.

9. LANDFILL GAS MONITORING

Monitoring Requirement

- 9.1 In accordance with the EM&A Manual, monitoring of landfill gas is required for construction works within the Sai Tso Wan Landfill Consultation Zone during the construction phase. This section presents the results of landfill gas measurements performed by the Contractor. **Appendix A** shows the Limit Levels for the monitoring works.
- 9.2 The “Landfill Gas Monitoring Proposal”, including the monitoring programme and detailed actions, is submitted to the EPD for approval. Details of monitoring in this Proposal is in line with the monitoring requirements stipulated in the EM&A Manual.

Monitoring Parameters and Frequency

- 9.3 Monitoring parameters for Landfill gas monitoring include Methane, Carbon dioxide and Oxygen.
- 9.4 According to the implementation schedule and recommended mitigation measures of the EM&A Manual, measurements of the following frequencies should be carried out:

Excavations deeper than 1m

- at the ground surface before excavation commences;-
- immediately before any worker enters the excavation;
- at the beginning of each working day for the entire period the excavation remains open; and
- periodically throughout the working day whilst workers are in the excavation.

Excavations between 300mm and 1m deep

- directly after the excavation has been completed; and
- periodically whilst the excavation remains open.

For excavations less than 300mm deep

- monitoring may be omitted, at the discretion of the Safety Officer or other appropriately qualified person

Monitoring Locations

- 9.5 Monitoring of oxygen, methane and carbon dioxide was performed for excavations at 1m depth or more within the Consultation Zone. In this reporting month, the area required to be monitored for landfill gas are shown below and **Figure 6** shows the landfill gas monitoring locations.
- | | |
|-----------------------------------|-------------|
| ➤ Excavation Locations: | Portion III |
| ➤ Manholes and Chambers: | N/A |
| ➤ Relocation of monitoring wells: | N/A |
| ➤ Any other Confined Spaces: | N/A |

Monitoring Equipment

- 9.6 **Table 9.1** summarizes the equipment employed by the Contractor for the landfill gas monitoring.

Table 9.1 Landfill Gas Monitoring Equipment

| Equipment | Model and Make | Quantity |
|---|---|-----------------|
| Intrinsically safe, portable gas detector | Crowcon Tetra Portable Gas Detector (Serial No. 100486262/01-020) | 1 |

Results and Observations

- 9.7 In the reporting month, landfill gas monitoring was carried out by the Contractor at the aforesaid locations on 46 occasions. No Limit Level exceedance for landfill gas monitoring was recorded in the reporting month. The monitoring results are provided in **Appendix R**. Copies of calibration certificates are attached in **Appendix B**.

10. ENVIRONMENTAL AUDIT

Site Audits

- 10.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix L**.
- 10.2 Joint weekly site audits by the representatives of the Engineer, Contractor and the ET were conducted in the reporting month as shown in below:
- Contract No. NE/2015/01: 4, 11, 18 and 25 October 2017
 - Contract No. NE/2015/02: 6, 12, 17 and 26 October 2017
 - Contract No. NE/2015/03: 6, 09, 19 and 26 October 2017
- Monthly joint site inspection with the representative of IEC was conducted for NE/2015/01, NE/2015/02 and NE/2015/03 on 25, 26 and 09 October 2017 respectively.

Implementation Status of Environmental Mitigation Measures

- 10.3 According to the EIA Study Report, Environmental Permit and the EM&A Manual of the Project, the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An updated summary of the Implementation Schedule and Recommended Mitigation Measures is provided in **Appendix N**.
- 10.4 During site inspections in the reporting month, no non-conformance was identified. The observations and recommendations made during the audit sessions are summarized in **Appendix L**.

11. WASTE MANAGEMENT

- 11.1 Waste generated from this Project includes inert construction and demolition (C&D) materials, non-inert C&D materials and marine sediments. Inert C&D waste includes soil, broken rock, broken concrete and building debris, while non-inert C&D materials are made up of C&D waste which cannot be reused or recycled and has to be disposed of at the designated landfill sites. Marine sediment shall be expected from excavation and dredging works of this Project.
- 11.2 With reference to relevant handling records of this Project, the quantities of different types of waste generated in the reporting month are summarised and presented in **Appendix P**.
- 11.3 The Contractors are advised to minimize the wastes generated through the recycling or reusing. All mitigation measures stipulated in the approved EM&A Manual and waste management plans shall be fully implemented. The status of implementation of waste management and reduction measures are submitted in **Appendix N**.

12. ENVIRONMENTAL NON-CONFORMANCE

Summary of Exceedances

- 12.1 Five Action Level exceedance of noise monitoring was recorded due to the documented complaints received in the reporting month. One Limit Level exceedance of noise monitoring was recorded in the reporting month.
- 12.2 Should the monitoring results of the environmental monitoring parameters at any designated monitoring stations indicate that the Action / Limit Levels are exceeded, the actions in accordance with the Event and Action Plans in **Appendix M** be carried out.

Summary of Environmental Non-Compliance

- 12.3 No environmental non-compliance was recorded in the reporting month.

Summary of Environmental Complaint

- 12.4 Eight environmental complaints were received in the reporting month. The Cumulative Complaint Log since the commencement of the Project is presented in **Appendix O**. The investigation status and result is also reported in **Appendix O**.

Summary of Environmental Summon and Successful Prosecution

- 12.5 There was no successful environmental prosecution or notification of summons received since the Project commencement. The Cumulative Log for environmental summon and successful prosecution since the commencement of the Project is presented in **Appendix O**.

13. FUTURE KEY ISSUES

13.1 Tentative construction programmes for the next three months are provided in **Appendix Q**.

13.2 Major site activities to be undertaken for the next reporting period are summarized in **Table 13.1**.

Table 13.1 Summary Table for Site Activities in the next Reporting Period

| Contract No. | Project Title | Site Activities (November 2017) | |
|---------------------|---|---|---|
| NE/2015/01 | Tseung Kwan O - Lam Tin Tunnel - Main Tunnel and Associated Works | Lam Tin Interchange | 1) EHC2 U-Trough 2) Site Formation – Area 1G1, Area 1G2, 2, 3, 4 & Area 5 3) Pipe Pile wall – Area 2A |
| | | Main Tunnel | 1) Main Tunnel Excavation |
| | | TKO Interchange | 1) Haul Road Construction, Site Formation and Slope Works 2) Temporary Barging Facilities & Temporary Platform 3) Temporary Cut Slope For BMCP 4) Steel Platform for Bridge Construction |
| NE/2015/02 | Tseung Kwan O – Lam Tin Tunnel – Road P2 and Associated Works | Portion I and III | 1) Earth pits, drainage and reinstatement works; 2) Chain link fence and road signages installation; 3) Demolition of the existing transformer room in Portion III |
| | | Portion IV and VII | 1) Pre-boring and sheet piling works; 2) Foot path and carriageway construction. |
| | | Portion V and VI | 1) Pre-bored socketed H-pile installation; 2) Dewatering system installation. |
| | | Portion VIII | 1) Construction of Retaining Wall 2) Excavation and Structural works for temporary steel cofferdam |
| | | Portion IX | 1) Dredging and reclamation Works 2) Seawall Construction 3) Placing sand blanket at non-dredged area |
| NE/2015/03 | Tseung Kwan O – Lam Tin Tunnel – Northern Footbridge | 1) Pile Construction at East Pier 2) Pile Cap Construction (with ELS) at East Pier | |

Key Issues for the Coming Month

13.3 Key environmental issues in the coming month include:

- Watering for dust generation from haul road, stockpiles of dusty materials, exposed site area, excavation works and rock breaking activities;
- Noisy construction activity such as rock-breaking activities and piling works;
- Runoff from exposed slope or site area;
- Wastewater and runoff discharge from site;
- Accumulation of silt, mud and sand along U-channels and sedimentation tanks;
- Set up and implementation of temporary drainage system for the surface runoff;
- Storage of chemicals/fuel and chemical waste/waste oil on site;
- Accumulation and storage of general and construction waste on site; and
- Marine water quality impact and indirect impact to coral communities due to marine construction for TKO-LTT reclamation.

Monitoring Schedule for the Next Month

13.4 The tentative environmental monitoring schedules for the next month are shown in **Appendix D**.

14. CONCLUSIONS AND RECOMMENDATIONS

Conclusions

- 14.1 This is the 12th Environmental Monitoring and Audit (EM&A) Report which presents the EM&A works undertaken during the period in October 2017 in accordance with EM&A Manual and the requirement under EP.

Air Quality Monitoring

- 14.2 All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 14.3 All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

Construction Noise Monitoring

- 14.4 All noise monitoring was conducted as scheduled in the reporting month. Five Action Level exceedance was recorded due to the documented complaints received in the reporting month. One Limit Level exceedance was recorded in the reporting month.

Water Quality Monitoring

- 14.5 Groundwater monitoring was conducted as scheduled in the reporting month. One Action Level exceedance was recorded in the reporting month which is considered to be non-Project related.
- 14.6 All marine water monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

Ecological Monitoring

- 14.7 Fourth post-translocation coral monitoring survey is scheduled to be carried out in November 2017 tentatively.

Monitoring on Cultural Heritage

- 14.8 No Alert Alarm and Action (AAA) Level exceedance of vibration monitoring on cultural heritage was recorded in the reporting month.

Landscape and Visual Monitoring and Audit

- 14.9 No non-compliance of the landscape and visual impact was recorded in the reporting month.

Landfill Gas Monitoring

- 14.10 Monitoring of landfill gases in the reporting month was carried out by the Contractor at excavation location, Portion III. No Limit Level exceedance was recorded.

Environmental Site Inspection

- 14.11 Joint weekly site inspections were conducted by representatives of the Contractor, Engineer and Environmental Team. During site inspections in the reporting month, no non-compliance was identified.

Complaint, Prosecution and Notification of Summons

- 14.12 Eight environmental complaint, no successful prosecution or notification of summons were received during the reporting period.

Recommendations

- 14.13 The following recommendations were made to the Contractor for the reporting month:

Air Quality Impact

- To implement dust suppression measures such as water spray on all haul roads, stockpiles, dry surfaces and open slopes.
- To cover stockpile of dusty material by impervious material.
- To avoid dark smoke emitted from the generator.

Construction Noise

- To provide noise mitigation measures (e.g. Temporary noise barrier or Full enclosure) to PME as proposed in the approved Noise Mitigation Plan.
- To repair the gaps between the noise barriers.

Water Quality Impact

- To provide and repair the silt curtain to fully enclose the site and prevent any gap between the silt curtains.
- To review and implement temporary drainage system.
- To clear the litter, debris, silt and sediment in drainage or catchpits.
- To remove the sand or dusty material deposited near the seafront.
- To provide bund or covers to gullies and stockpile storage area on site to avoid leakage of surface runoff.
- To divert all the water generated from construction site to de-silting facilities with enough handling capacity before discharge.
- To maintain the sedimentation tank more frequently to ensure proper wastewater treatment before discharge.


Waste/Chemical Management

- To remove construction waste regularly.
- To avoid any discharge or accidental spillage of chemical waste or oil directly from the equipment.
- To provide drip tray to chemical containers to avoid any chemical leakage.
- To remove the oil stain and disposed of as chemical waste.
- To remove the stagnant water regularly found inside the drip tray.

Landscape and Visual

- To set up proper tree protection area.
- To avoid placing any construction materials in the tree protection zone.

FIGURES

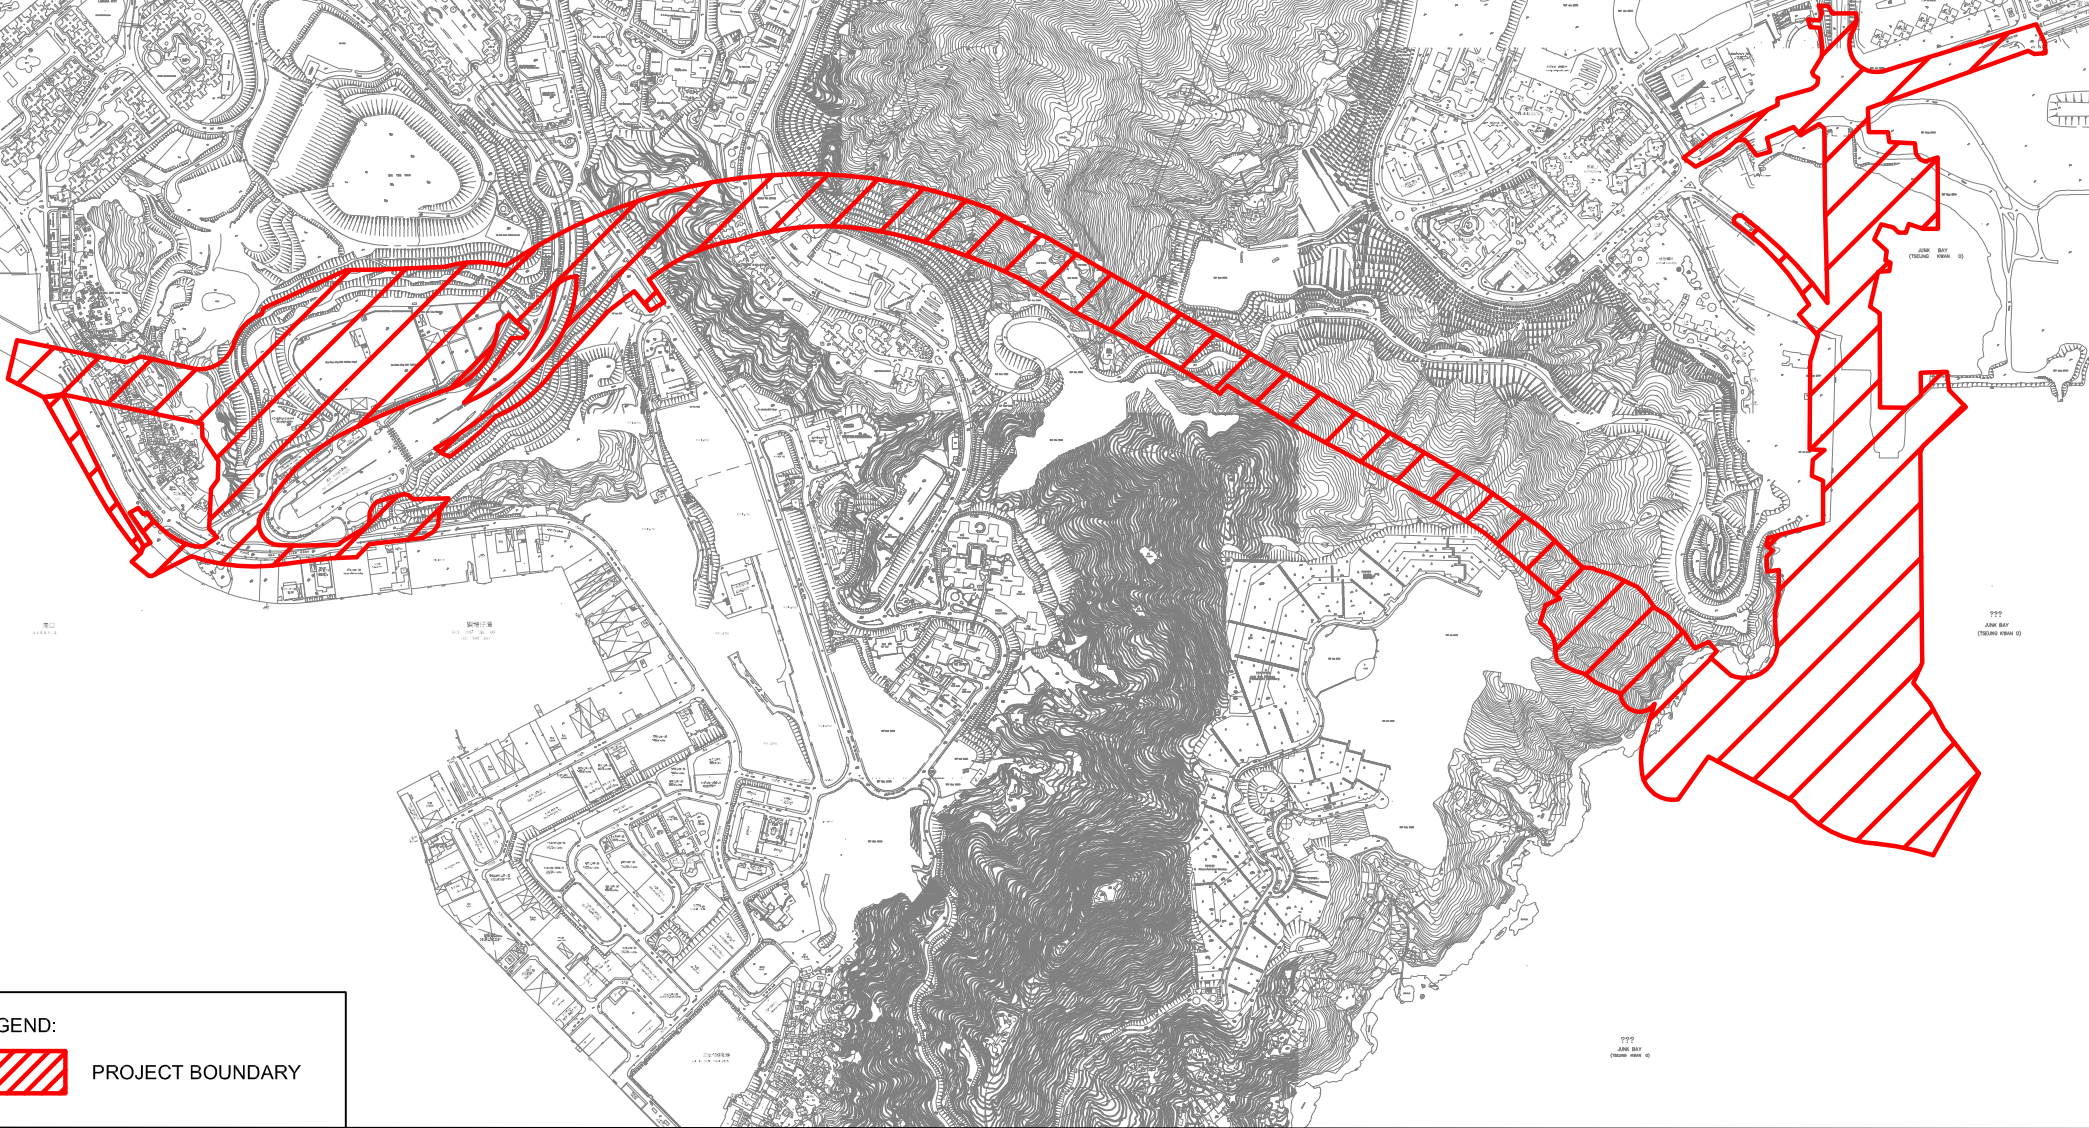


LEGEND:

 PROJECT BOUNDARY


CINOTECH
Cinotech Consultants Limited

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel
- Design and Construction
Site Layout Plan

| | | | | |
|---------|--------------|------------|----------|-----|
| SCALE | 1:15000 @ A4 | DATE | APR 2017 | |
| CHECK | JF | DRAWN | JW | |
| JOB No. | MA16034 | FIGURE NO. | 1 | REV |
| | | | | - |

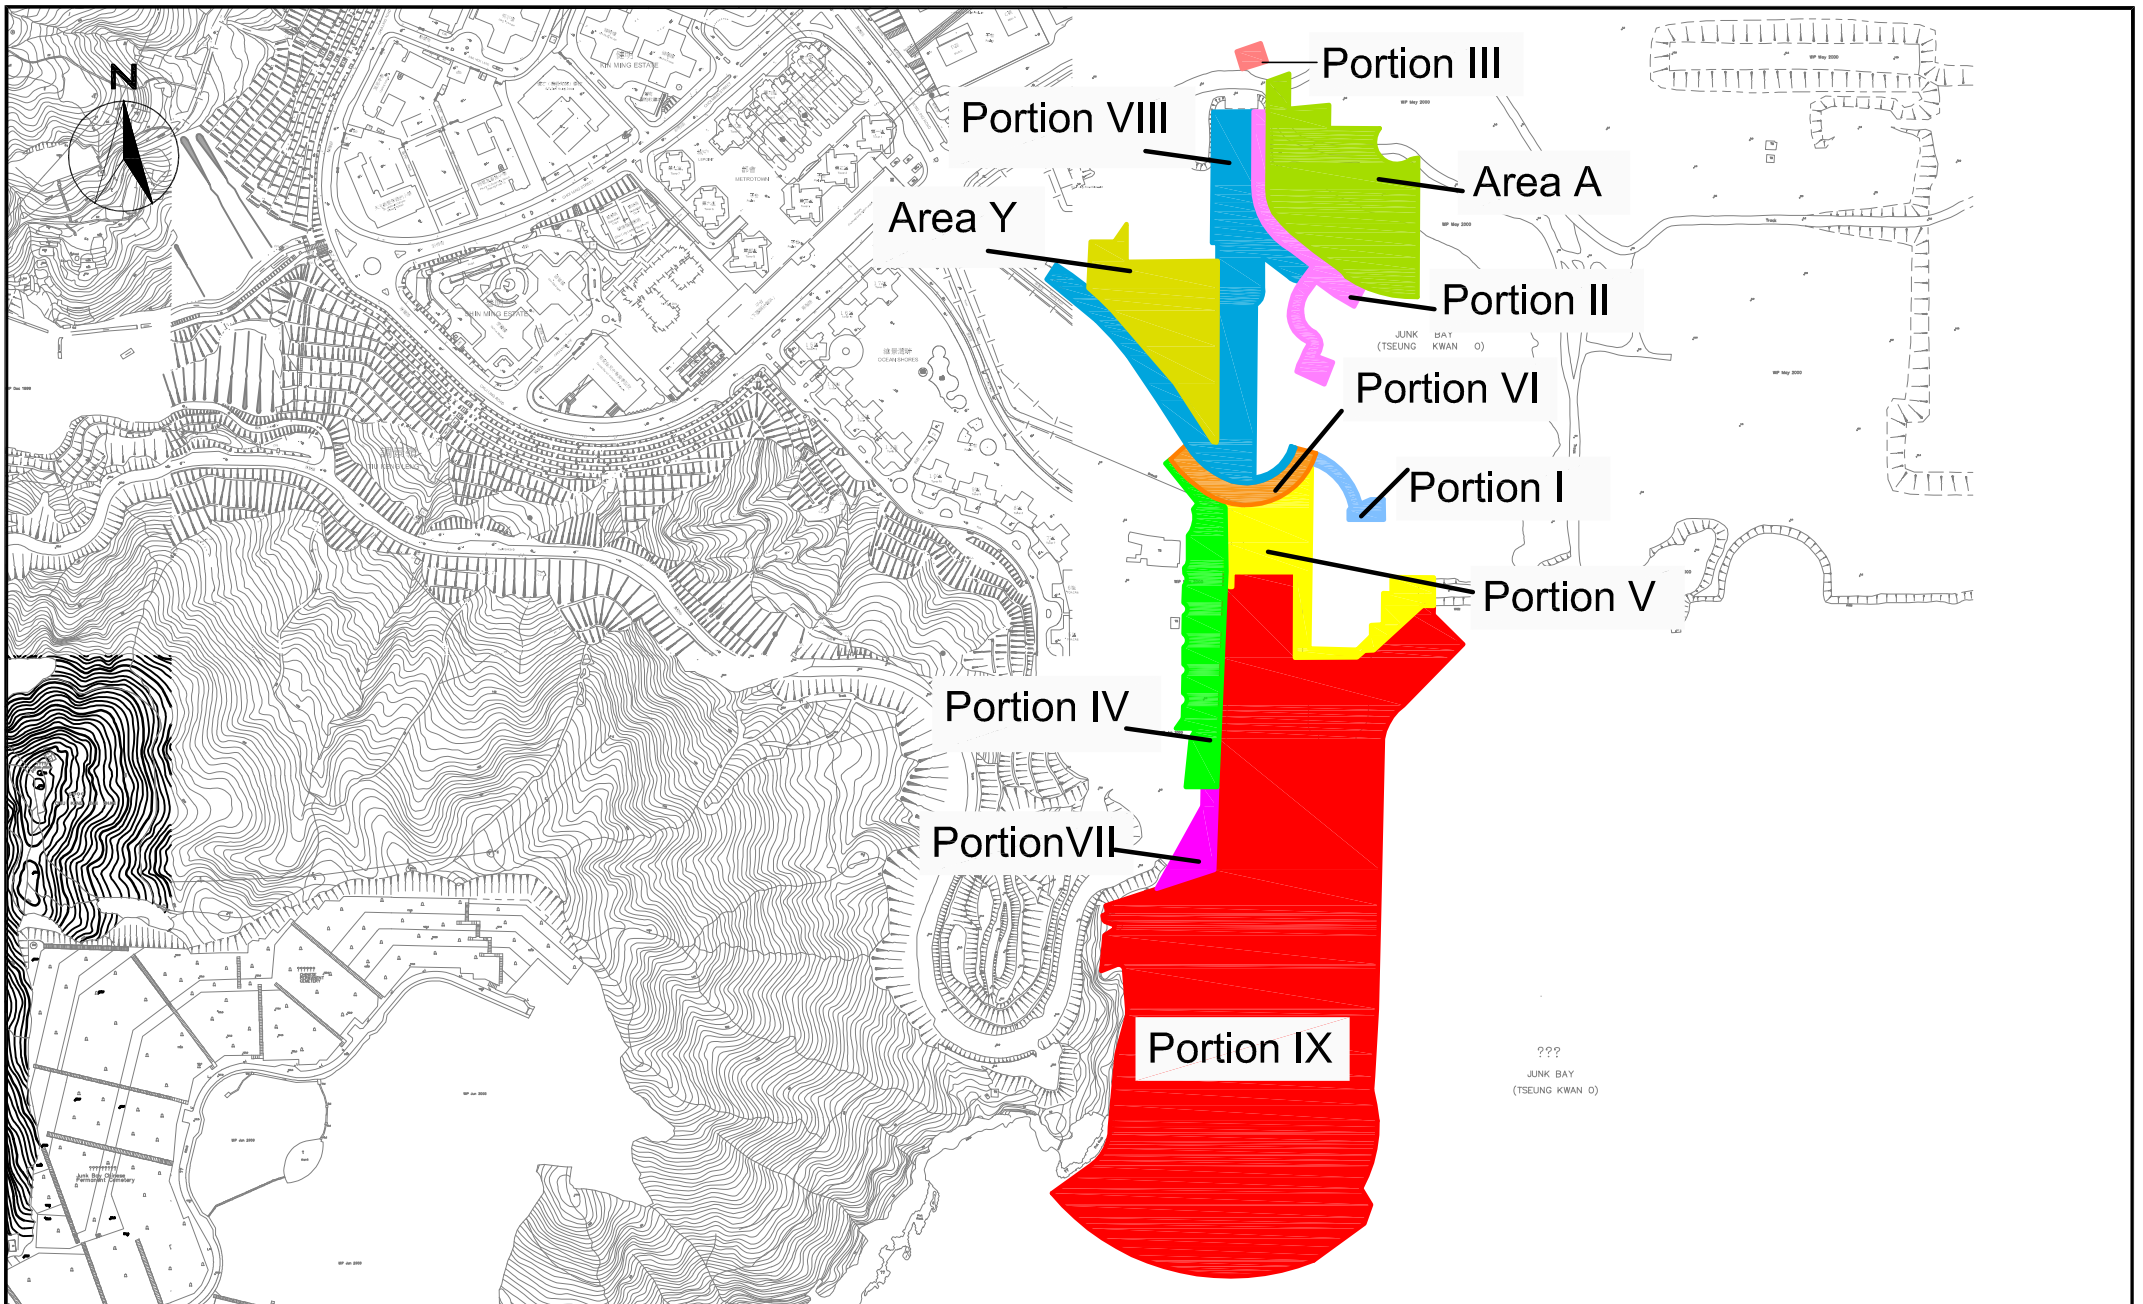

| | | | | |
|---------|---------|------------|----------|----------|
| SCALE | N.T.S. | DATE | AUG 2017 | |
| CHECK | JF | DRAWN | JW | |
| JOB No. | MA16034 | FIGURE NO. | 1a | REV - |

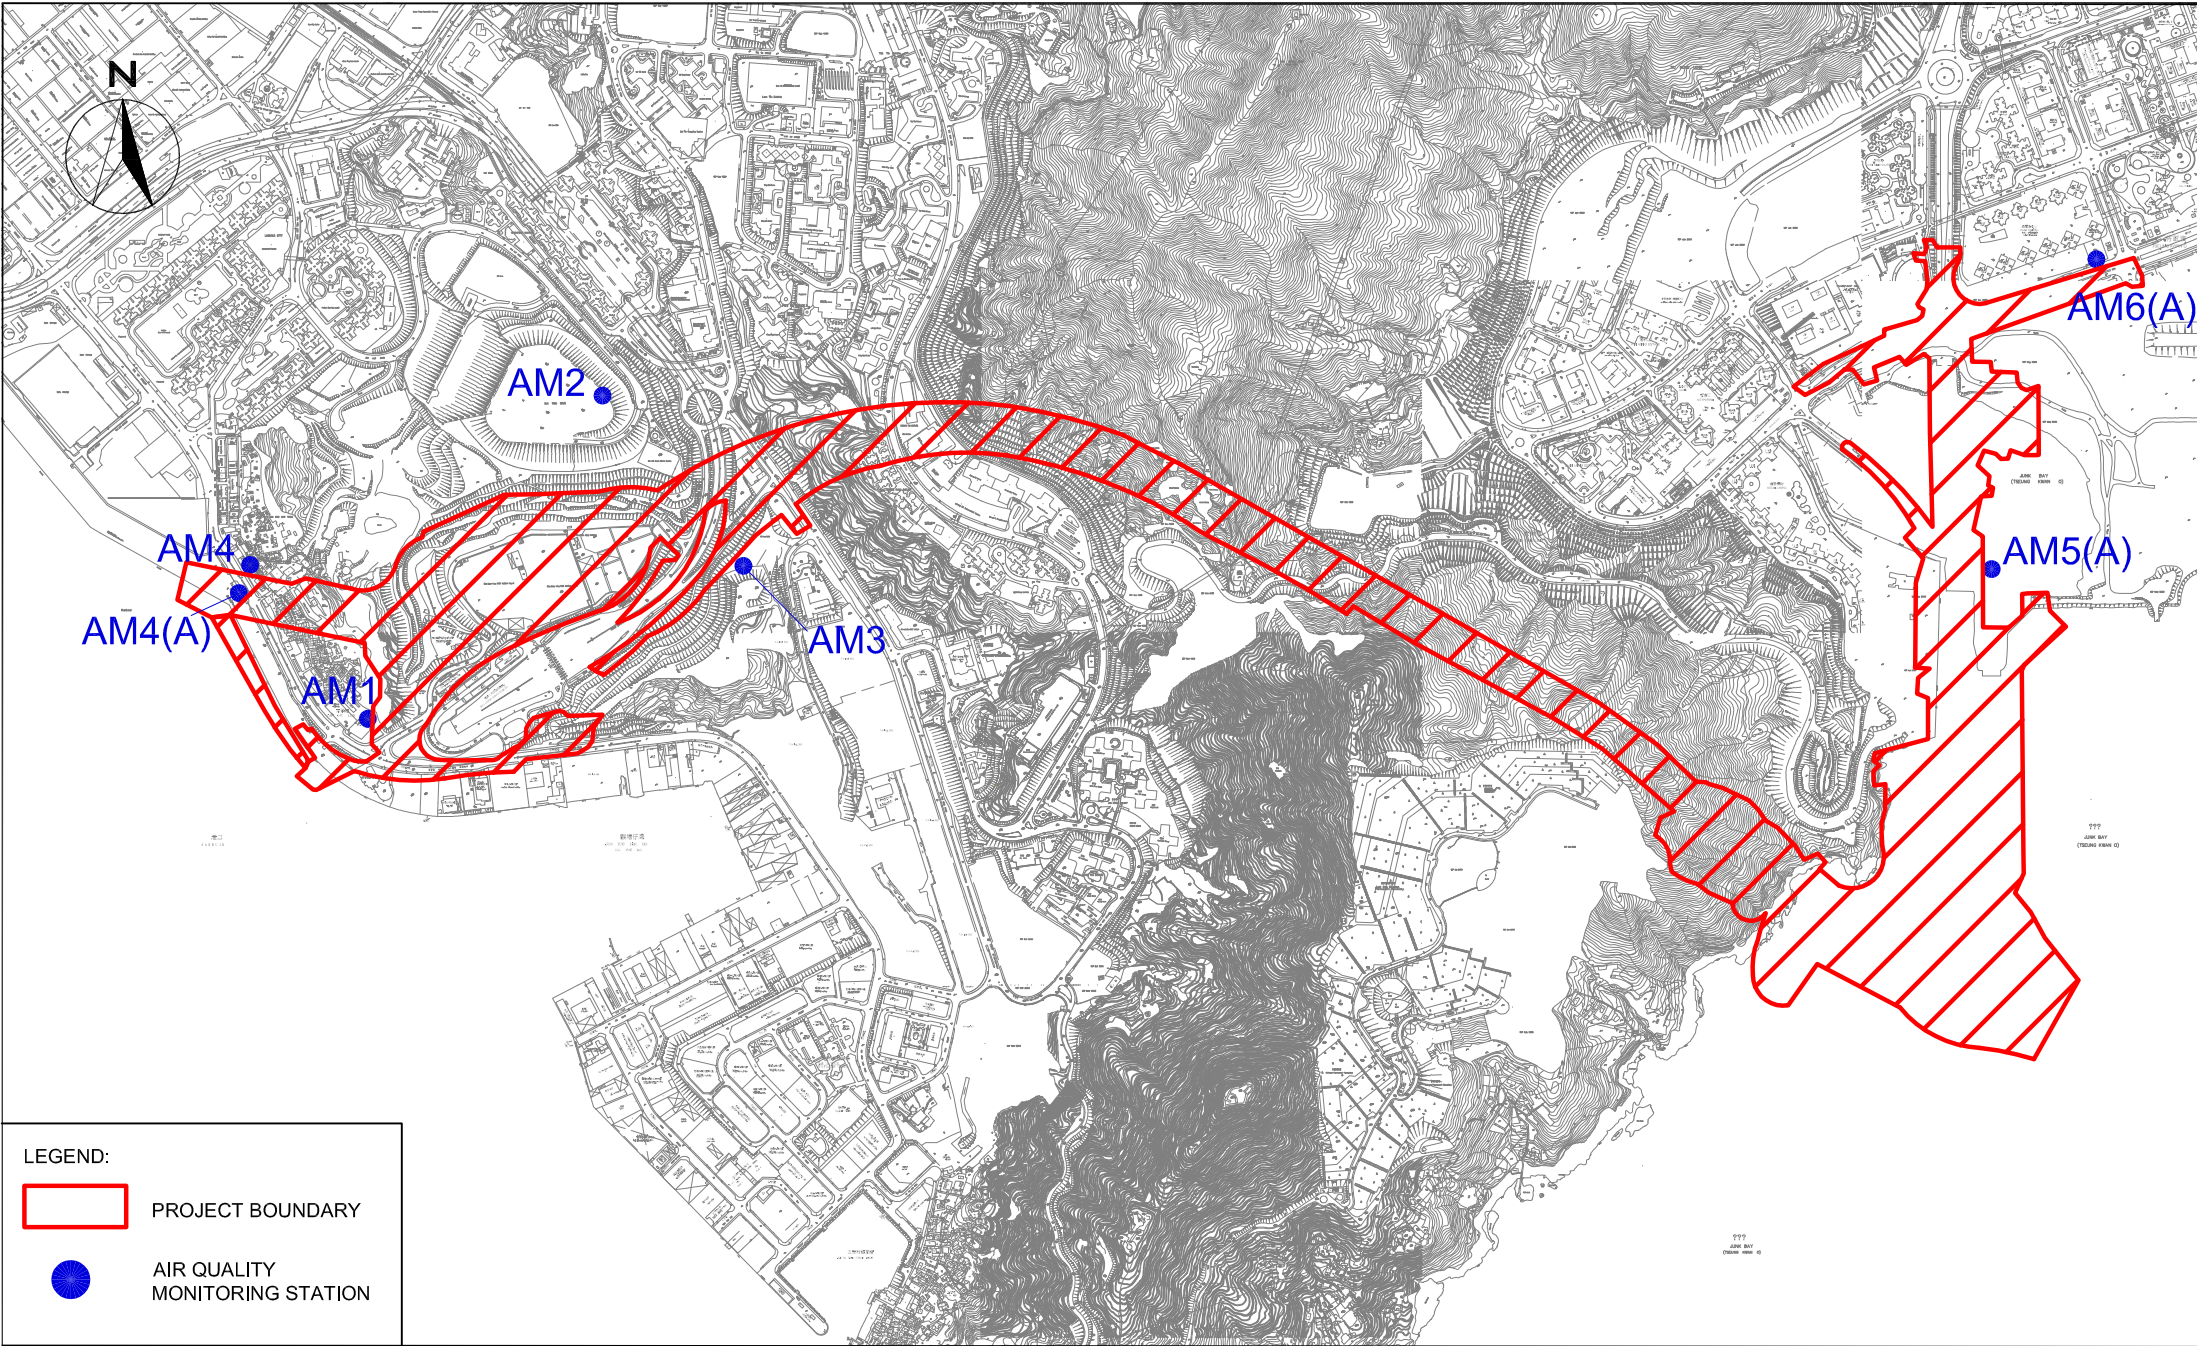


LEGEND:

- PROJECT BOUNDARY
- AIR QUALITY MONITORING STATION



Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel -
 Design and Construction
 Air Quality Monitoring Stations

| | | | | |
|---------|--------------|------------|----------|-----|
| SCALE | 1:15000 @ A4 | DATE | APR 2017 | |
| CHECK | JF | DRAWN | JW | |
| JOB No. | MA16034 | FIGURE NO. | 2 | REV |
| | | | - | |

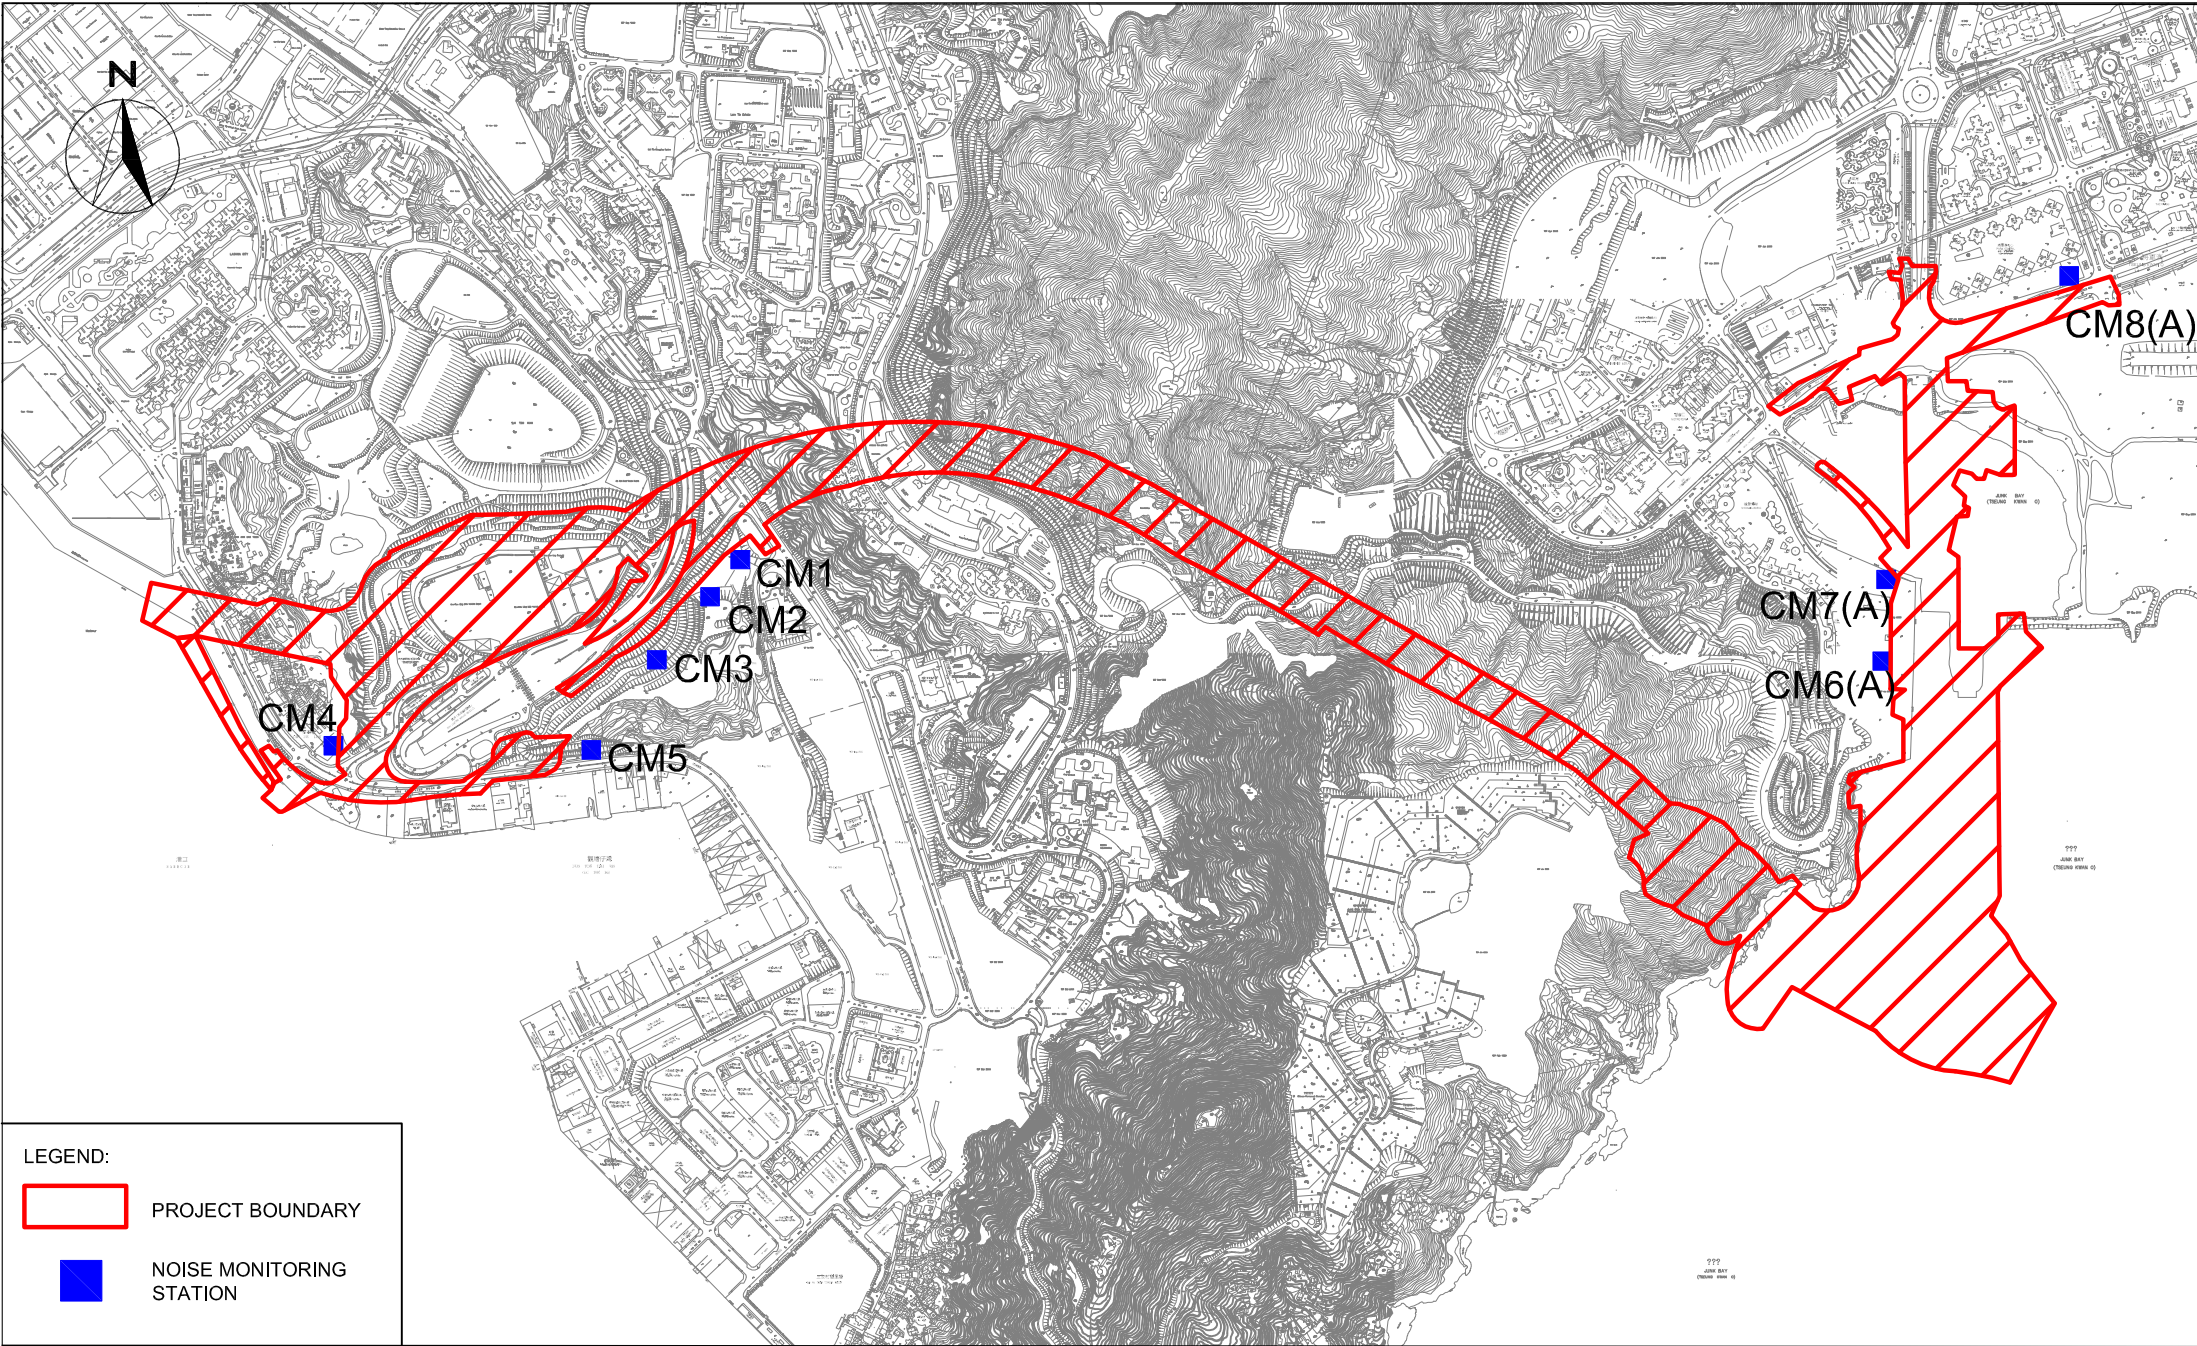


LEGEND:

- PROJECT BOUNDARY
- NOISE MONITORING STATION





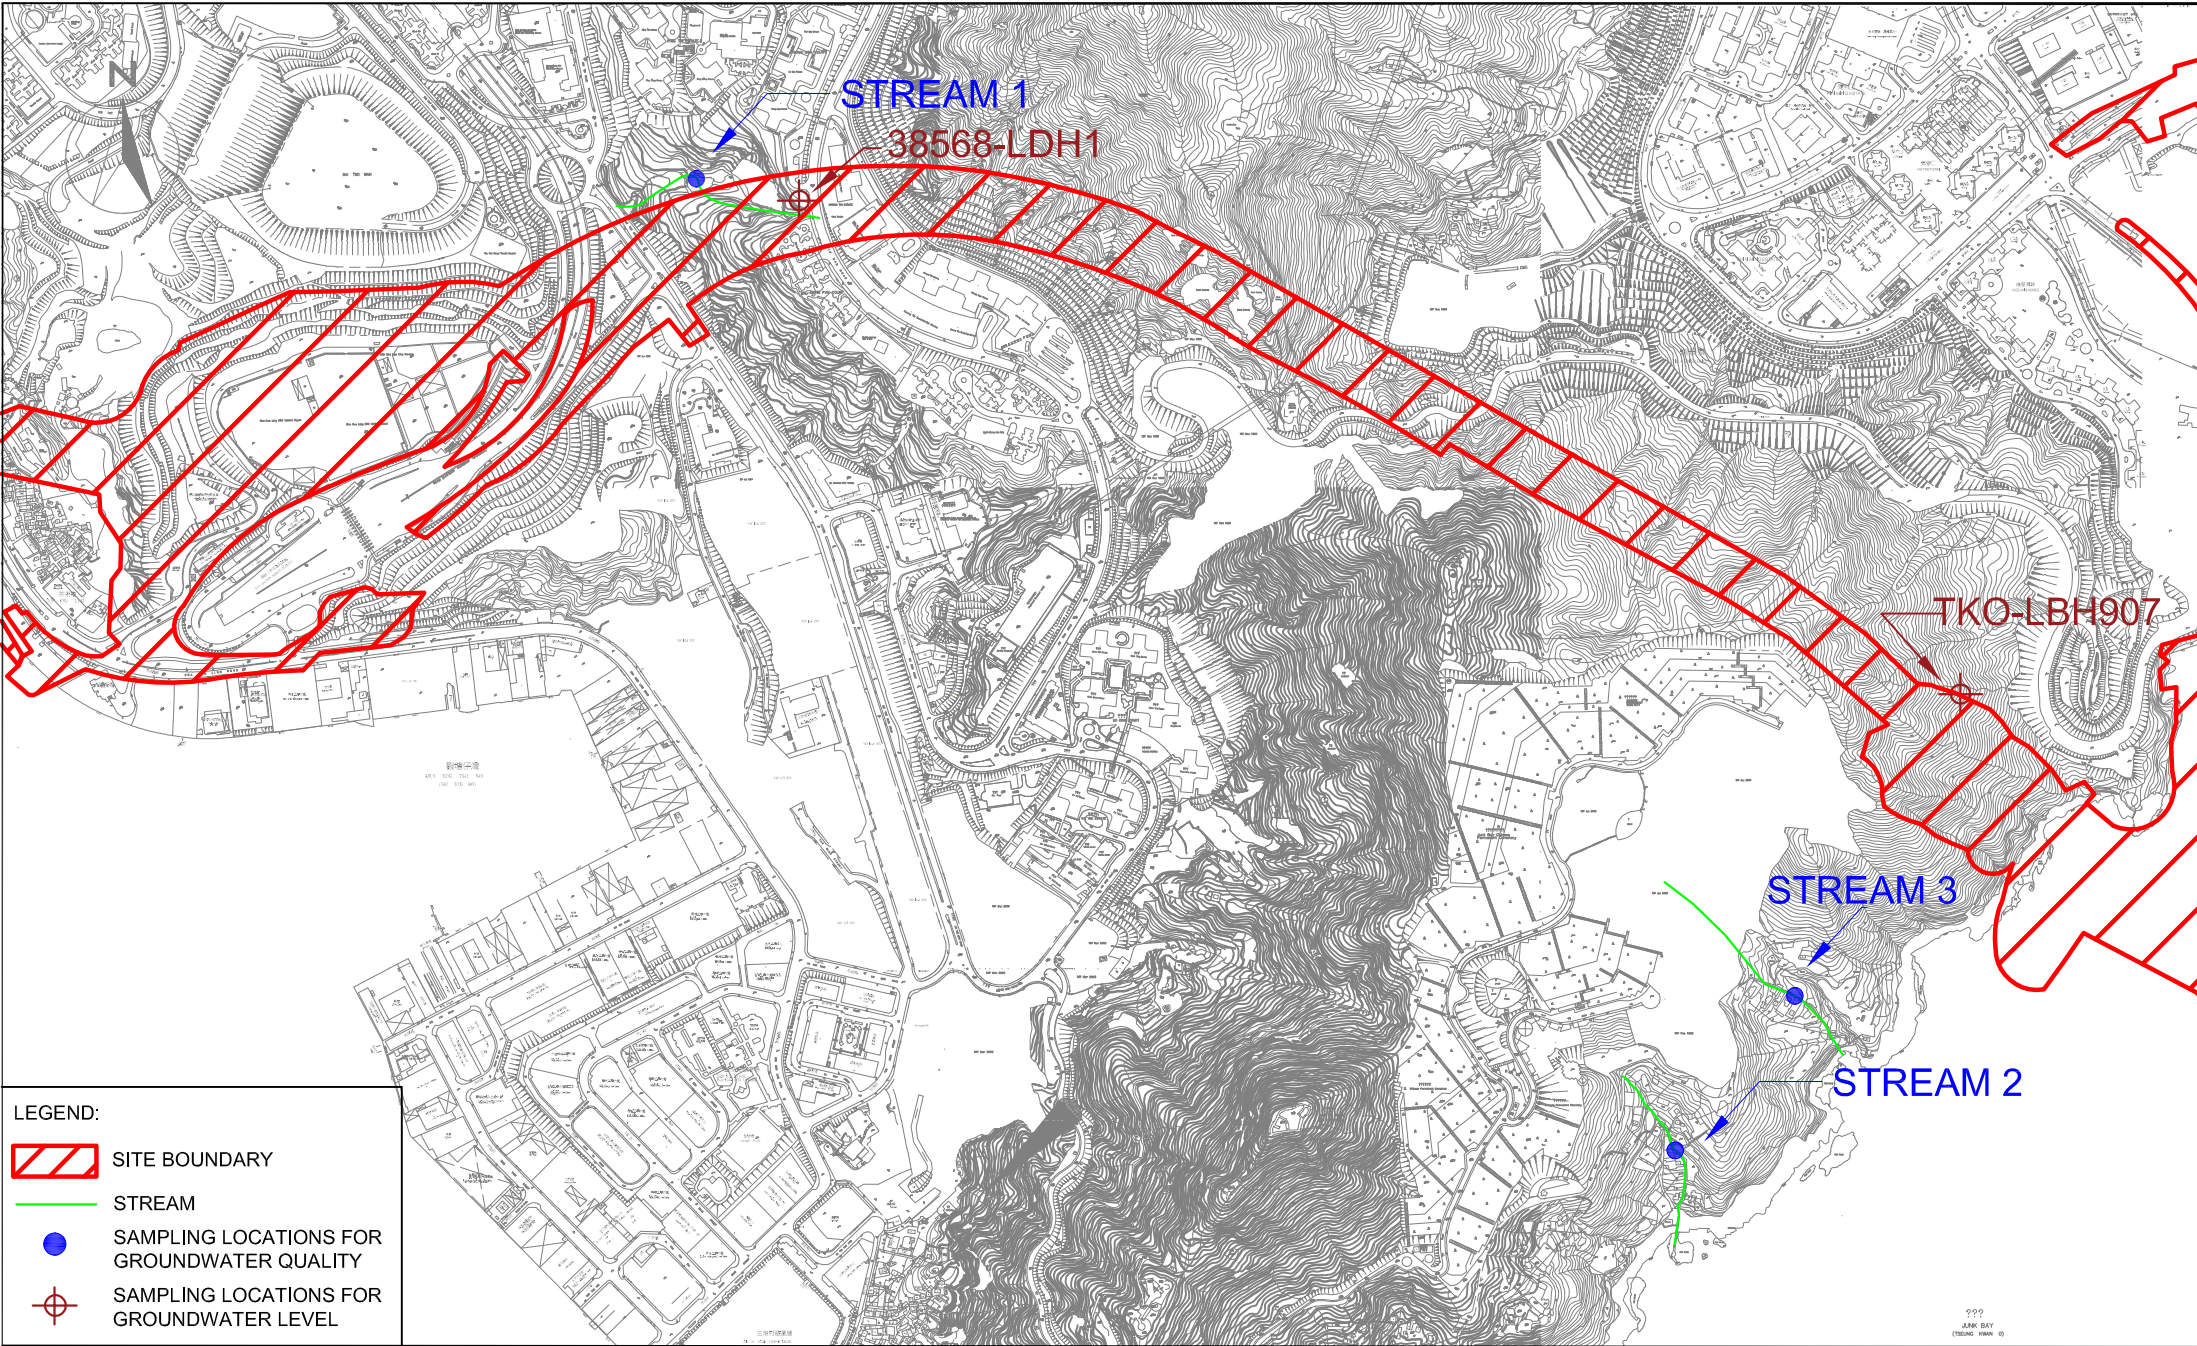

Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel -
 Design and Construction
 Noise Monitoring Stations

| | | | | |
|---------|--------------|------------|----------|-----|
| SCALE | 1:15000 @ A4 | DATE | APR 2017 | |
| CHECK | JF | DRAWN | JW | |
| JOB No. | MA16034 | FIGURE NO. | 3 | REV |
| | | | - | |




LEGEND:

-  SITE BOUNDARY
-  STREAM
-  SAMPLING LOCATIONS FOR GROUNDWATER QUALITY
-  SAMPLING LOCATIONS FOR GROUNDWATER LEVEL



Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel -
 Design and Construction
 Location of Streams for Groundwater Quality and Groundwater Level Monitoring

| | | | | |
|---------|--------------|------------|----------|-----|
| SCALE | 1:10000 @ A4 | DATE | APR 2017 | |
| CHECK | JF | DRAWN | JW | |
| JOB No. | MA16034 | FIGURE NO. | 4 | REV |
| | | | | - |

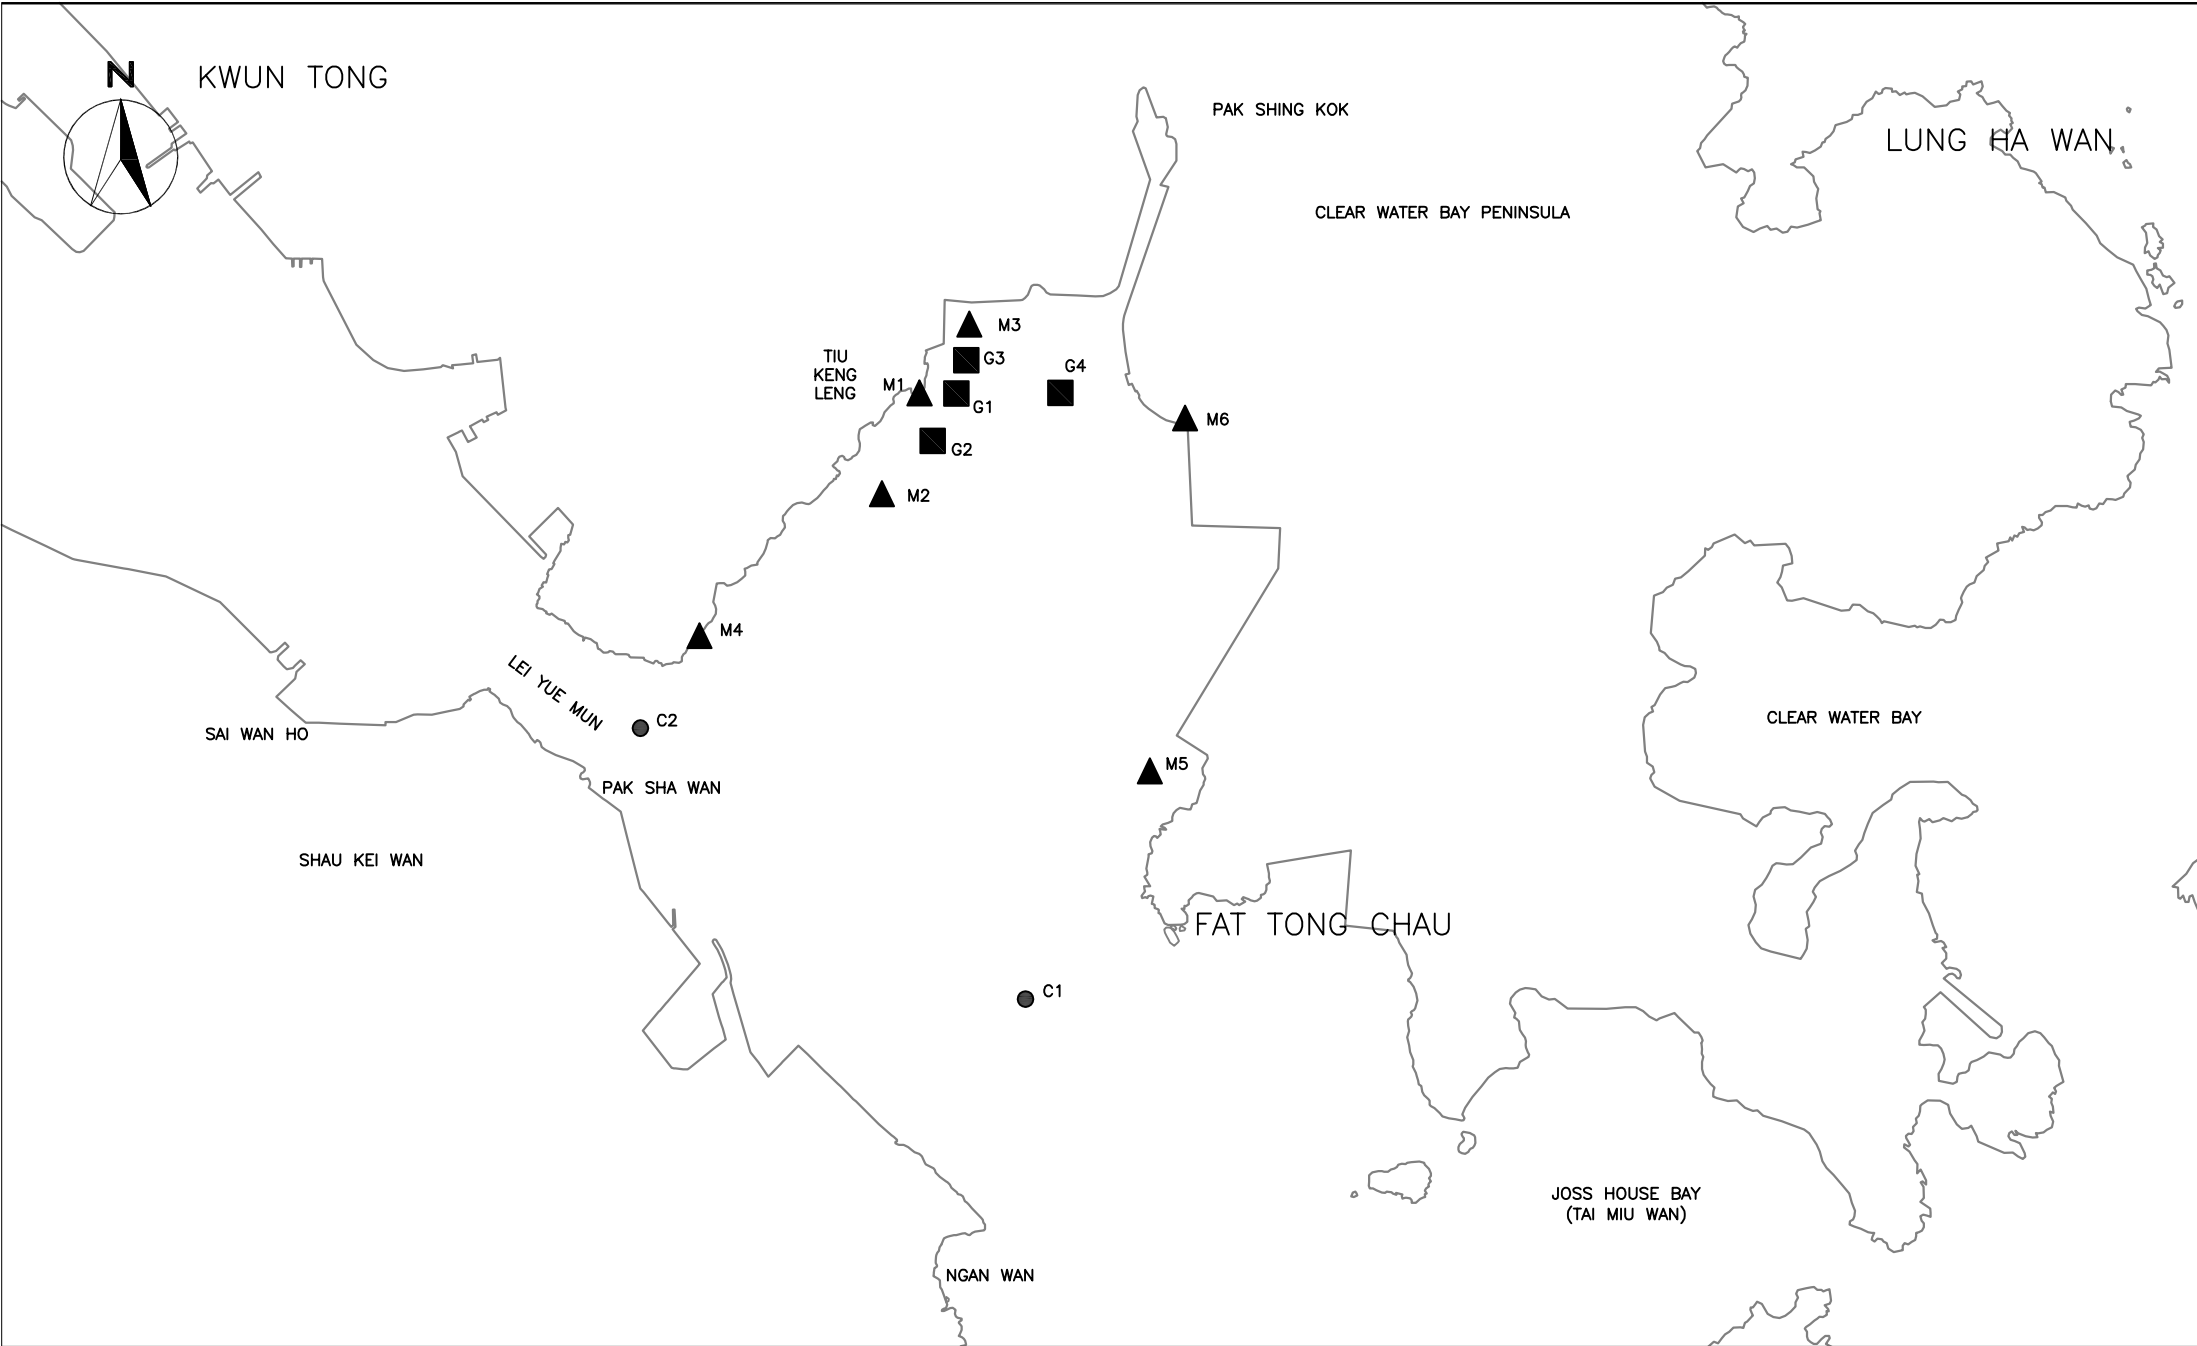

| | | | | |
|-------------|---------|------------|----------|----------|
| SCALE | N.T.S | DATE | AUG 2016 | |
| CHECK | JF | DRAWN | JW | |
| PROJECT NO. | MA16034 | FIGURE NO. | 5 | REV — |



Title Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
 Locations of Landfill Gas Monitoring

Scale N.T.S
 Date Dec-16

Project No. MA16034
 Figure 6





Cha Kwo Ling Tin Hau Temple




Child Giving Rock

No works in this area (in blue color) in the reporting peiod.

Temporary Location of Vibration Monitoring

LEGEND

- - - SITE BOUNDARY
- - - 100M FROM THE CHA KWO LING TIN HAU TEMPLE
- CHA KWO LING TIN HAU TEMPLE
- ⊕ VIBRATION MONITORING POINT
- ⊗ BUILDING SETTLEMENT POINT
- ⊘ TILTMETER

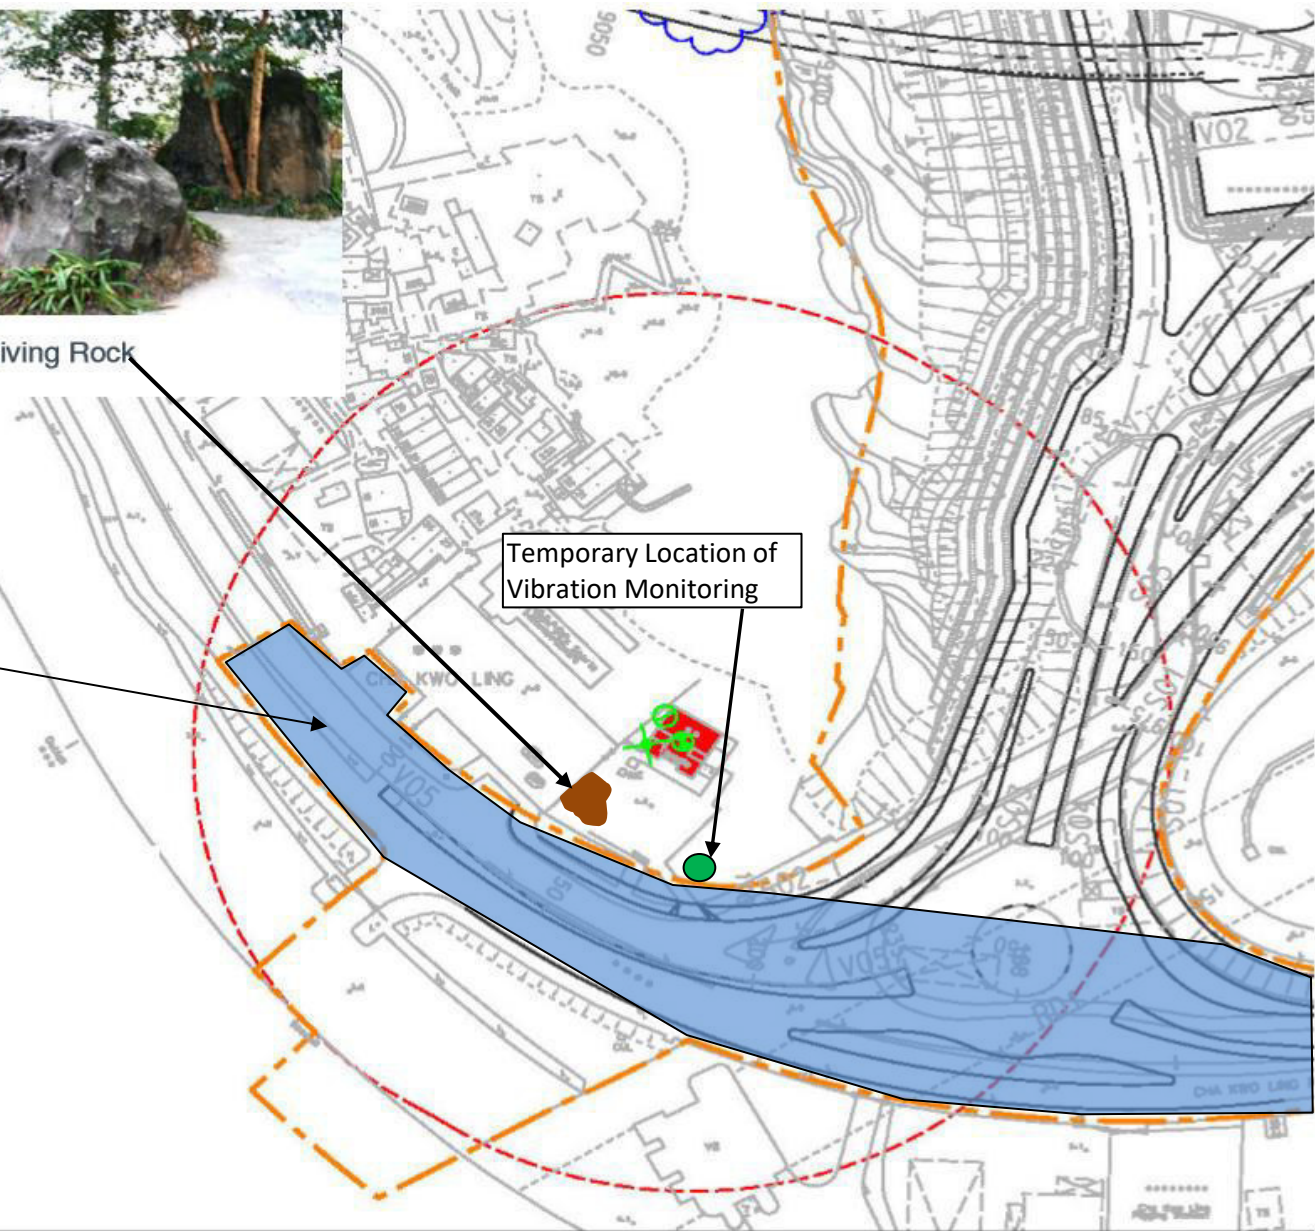

Title Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
 Locations of Monitoring for Cultural Heritage

| | | | |
|-------|--------|-------------|---------|
| Scale | N.T.S | Project No. | MA16034 |
| Date | Apr-17 | Figure | 8 |



**APPENDIX A
ACTION AND LIMIT LEVELS**

APPENDIX A – Action and Limit Levels**Air Quality*****1-hr TSP***

| Monitoring Stations | Location | Action Level, $\mu\text{g}/\text{m}^3$ | Limit Level, $\mu\text{g}/\text{m}^3$ |
|---------------------|--|--|---------------------------------------|
| AM1 | Tin Hau Temple | 275 | 500 |
| AM2 | Sai Tso Wan Recreation Ground | 273 | |
| AM3 | Yau Lai Estate Bik Lai House | 271 | |
| AM4 | Sitting-out Area at Cha Kwo Ling Village | 278 | |
| AM5(A) | Tseung Kwan O DSD Desilting Compound | 273 | |
| AM6(A) | Park Central, L1/F Open Space Area | 285 | |

24-hr TSP

| Monitoring Stations | Location | Action Level, $\mu\text{g}/\text{m}^3$ | Limit Level, $\mu\text{g}/\text{m}^3$ |
|---------------------|---|--|---------------------------------------|
| AM1 | Tin Hau Temple | 173 | 260 |
| AM2 | Sai Tso Wan Recreation Ground | 192 | |
| AM3 | Yau Lai Estate Bik Lai House | 167 | |
| AM4(A) | Cha Kwo Ling Public Cargo Working Area Administrative Office | 210 | |
| AM5(A) | Tseung Kwan O DSD Desilting Compound | 175 | |
| AM6(A) | Park Central, L1/F Open Space Area | 165 | |

Noise

| Time Period | Action Level | Limit Level |
|---|---|----------------------------------|
| 0700-1900 hrs on normal weekdays | When one documented complaint is received | 75 dB(A) ⁽¹⁾ |
| 1900-2300 on all days and 0700-2300 on general holidays (including Sundays) | | 60/65/70 dB(A) ⁽²⁾⁽³⁾ |
| 2300-0700 on all days | | 45/50/55 dB(A) ⁽²⁾⁽³⁾ |

¹ 70 dB(A) for schools and 65 dB(A) for schools during examination period.² Acceptable Noise Levels for Area Sensitivity Rating of A/B/C³ If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.

Water Quality***Groundwater***

| Parameters | Action | Limit |
|--|--------------------------|--------------------------|
| DO in mg L ⁻¹ | 7.6 | 7.6 |
| pH | 6.0 – 8.9 | 6.0 – 9.0 |
| BOD ₅ in mg L ⁻¹ | 2.0 | 2.0 |
| TOC in mg L ⁻¹ | Stream 1 and Stream 2: 9 | Stream 1 and Stream 2: 9 |
| | Stream 3: 6 | Stream 3: 6 |
| Total Nitrogen in mg L ⁻¹ | 2.0 | 2.1 |
| Ammonia-N in mg L ⁻¹ | 0.15 | 0.20 |
| Total Phosphate in mg L ⁻¹ | 0.05 | 0.05 |
| SS in mg L ⁻¹ | 7.6 | 12.1 |
| Turbidity in NTU | 2.1 | 2.3 |

Notes:

1. For pH, non-compliance of the water quality limits occurs when monitoring result is out of the range of the limits.
2. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
3. For turbidity, SS, 5-day biochemical oxygen demand (BOD₅), Total organic carbon (TOC), Total Nitrogen, Ammonia-N and Total Phosphate, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
4. All the figures given in the table are used for reference only and the EPD may amend the figures whenever it is considered as necessary.

Groundwater Level Monitoring

| Drill Hole No. | 38568-LDH1 | TKO-LBH907 |
|-----------------------|-------------------|-------------------|
| Action Level (mPD) | +74.65 | +17.59 |

Marine Water Quality

| Parameter (unit) | Depth | Action Level | Limit Level |
|--|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2, 4 and 5) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| SS in mg/L (See Note 2, 4 and 5) | <u>Stations G1-G4</u> | | |
| | Surface | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day | <u>6.9mg/L</u> or 130% of upstream control station's SS at the same tide of the same day |
| | <u>Stations M1-M5</u> | | |
| | Surface | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day |
| | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day |
| | <u>Station M6</u> | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.
5. Refer to Appendix I – Marine Water Quality Monitoring Results and Graphical Presentations for results of upstream control stations at each tide on each day.

Ecology***Post-translocation Coral Monitoring***

| Parameter | Action Level Definition | Limit Level Definition |
|------------------|---|---|
| Mortality | If during Impact Monitoring a 15% increase in the percentage of partial mortality on hard corals occurs at more than 20% of the tagged coral at any one Impact Monitoring Site that is not recorded at the Control Site, then the Action Level is exceeded. | If during the Impact Monitoring a 25% increase in the percentage of partial mortality occurs at more than 20% of the tagged coral at any one Impact Monitoring Site that is not recorded at the Control Site, then the Limit Level is exceeded. |

Landfill Gas Monitoring

| Parameter | Limit Level |
|------------------|----------------------------------|
| Oxygen | <19% |
| | <18% |
| Methane | >10% LEL (i.e. > 0.5% by volume) |
| | >20% LEL (i.e. > 1% by volume) |
| Carbon Dioxide | >0.5% |
| | >1.5% |

**APPENDIX B
COPIES OF CALIBRATION
CERTIFICATES**

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/170818 |
| Date of Issue: | 2017-08-21 |
| Date Received: | 2017-08-18 |
| Date Tested: | 2017-08-18 |
| Date Completed: | 2017-08-21 |
| Next Due Date: | 2017-10-20 |

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

| | |
|-----------------|-----------------------------|
| Description | : Handheld Particle Counter |
| Manufacturer | : Hal Technology |
| Model No. | : Hal-HPC300 |
| Serial No. | : 3020408 |
| Flow rate | : 0.1 cfm |
| Zero Count Test | : 0 count per 5 minutes |
| Equipment No. | : A-26-01 |

Test Conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 21 degree Celsius |
| Relative Humidity | : 62 % |

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

| | |
|-------------------------|-------|
| Correlation Factor (CF) | 1.119 |
|-------------------------|-------|

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/171020 |
| Date of Issue: | 2017-10-23 |
| Date Received: | 2017-10-20 |
| Date Tested: | 2017-10-20 |
| Date Completed: | 2017-10-23 |
| Next Due Date: | 2017-12-22 |

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description : Handheld Particle Counter
 Manufacturer : Hal Technology
 Model No. : Hal-HPC300
 Serial No. : 3020408
 Flow rate : 0.1 cfm
 Zero Count Test : 0 count per 5 minutes
 Equipment No. : A-26-01

Test Conditions:

Room Temperature : 20 degree Celsius
 Relative Humidity : 65 %

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

| | |
|-------------------------|-------|
| Correlation Factor (CF) | 1.117 |
|-------------------------|-------|

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/170818A |
| Date of Issue: | 2017-08-21 |
| Date Received: | 2017-08-18 |
| Date Tested: | 2017-08-18 |
| Date Completed: | 2017-08-21 |
| Next Due Date: | 2017-10-20 |

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description : Handheld Particle Counter
 Manufacturer : Hal Technology
 Model No. : Hal-HPC300
 Serial No. : 3020409
 Flow rate : 0.1 cfm
 Zero Count Test : 0 count per 5 minutes
 Equipment No. : A-26-02

Test Conditions:

Room Temperature : 21 degree Celsius
 Relative Humidity : 62 %

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

| | |
|-------------------------|-------|
| Correlation Factor (CF) | 1.114 |
|-------------------------|-------|

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/171020A |
| Date of Issue: | 2017-10-23 |
| Date Received: | 2017-10-20 |
| Date Tested: | 2017-10-20 |
| Date Completed: | 2017-10-23 |
| Next Due Date: | 2017-12-22 |

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

| | |
|-----------------|-----------------------------|
| Description | : Handheld Particle Counter |
| Manufacturer | : Hal Technology |
| Model No. | : Hal-HPC300 |
| Serial No. | : 3020409 |
| Flow rate | : 0.1 cfm |
| Zero Count Test | : 0 count per 5 minutes |
| Equipment No. | : A-26-02 |

Test Conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 20 degree Celsius |
| Relative Humidity | : 65 % |

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

| | |
|-------------------------|-------|
| Correlation Factor (CF) | 1.076 |
|-------------------------|-------|

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/171013 |
| Date of Issue: | 2017-10-16 |
| Date Received: | 2017-10-13 |
| Date Tested: | 2017-10-13 |
| Date Completed: | 2017-10-16 |
| Next Due Date: | 2017-12-15 |

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description : Handheld Particle Counter
 Manufacturer : Hal Technology
 Model No. : Hal-HPC301
 Serial No. : 3011701019
 Flow rate : 0.1 cfm
 Zero Count Test : 0 count per 5 minutes
 Equipment No. : A-27-01

Test Conditions:

Room Temperature : 21 degree Celsius
 Relative Humidity : 60 %

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

| | |
|-------------------------|-------|
| Correlation Factor (CF) | 1.152 |
|-------------------------|-------|

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/170811C |
| Date of Issue: | 2017-08-14 |
| Date Received: | 2017-08-11 |
| Date Tested: | 2017-08-11 |
| Date Completed: | 2017-08-14 |
| Next Due Date: | 2017-10-13 |

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

| | |
|-----------------|-----------------------------|
| Description | : Handheld Particle Counter |
| Manufacturer | : Hal Technology |
| Model No. | : Hal-HPC301 |
| Serial No. | : 3011701017 |
| Flow rate | : 0.1 cfm |
| Zero Count Test | : 0 count per 5 minutes |
| Equipment No. | : A-27-04 |

Test Conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 23 degree Celsius |
| Relative Humidity | : 64 % |

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

| | |
|-------------------------|-------|
| Correlation Factor (CF) | 1.181 |
|-------------------------|-------|

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/171013C |
| Date of Issue: | 2017-10-16 |
| Date Received: | 2017-10-13 |
| Date Tested: | 2017-10-13 |
| Date Completed: | 2017-10-16 |
| Next Due Date: | 2017-12-15 |

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description : Handheld Particle Counter
 Manufacturer : Hal Technology
 Model No. : Hal-HPC301
 Serial No. : 3011701017
 Flow rate : 0.1 cfm
 Zero Count Test : 0 count per 5 minutes
 Equipment No. : A-27-04

Test Conditions:

Room Temperature : 21 degree Celsius
 Relative Humidity : 60 %

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

| | |
|-------------------------|-------|
| Correlation Factor (CF) | 1.155 |
|-------------------------|-------|

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/170811F |
| Date of Issue: | 2017-08-14 |
| Date Received: | 2017-08-11 |
| Date Tested: | 2017-08-11 |
| Date Completed: | 2017-08-14 |
| Next Due Date: | 2017-10-13 |

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description : Handheld Particle Counter
 Manufacturer : Hal Technology
 Model No. : Hal-HPC301
 Serial No. : 3011701012
 Flow rate : 0.1 cfm
 Zero Count Test : 0 count per 5 minutes
 Equipment No. : A-27-07

Test Conditions:

Room Temperature : 23 degree Celsius
 Relative Humidity : 64 %

Test Specifications & Methodology:


1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

| | |
|-------------------------|-------|
| Correlation Factor (CF) | 1.184 |
|-------------------------|-------|

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/170811H |
| Date of Issue: | 2017-08-14 |
| Date Received: | 2017-08-11 |
| Date Tested: | 2017-08-11 |
| Date Completed: | 2017-08-14 |
| Next Due Date: | 2017-10-13 |

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

| | |
|-----------------|-----------------------------|
| Description | : Handheld Particle Counter |
| Manufacturer | : Hal Technology |
| Model No. | : Hal-HPC301 |
| Serial No. | : 3011701015 |
| Flow rate | : 0.1 cfm |
| Zero Count Test | : 0 count per 5 minutes |
| Equipment No. | : A-27-09 |

Test Conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 23 degree Celsius |
| Relative Humidity | : 64 % |

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

| | |
|-------------------------|-------|
| Correlation Factor (CF) | 1.095 |
|-------------------------|-------|

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/171013H |
| Date of Issue: | 2017-10-16 |
| Date Received: | 2017-10-13 |
| Date Tested: | 2017-10-13 |
| Date Completed: | 2017-10-16 |
| Next Due Date: | 2017-12-15 |

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

| | |
|-----------------|-----------------------------|
| Description | : Handheld Particle Counter |
| Manufacturer | : Hal Technology |
| Model No. | : Hal-HPC301 |
| Serial No. | : 3011701015 |
| Flow rate | : 0.1 cfm |
| Zero Count Test | : 0 count per 5 minutes |
| Equipment No. | : A-27-09 |

Test Conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 21 degree Celsius |
| Relative Humidity | : 60 % |

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

| | |
|-------------------------|-------|
| Correlation Factor (CF) | 1.095 |
|-------------------------|-------|

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/N/170915 |
| Date of Issue: | 2017-09-18 |
| Date Received: | 2017-09-15 |
| Date Tested: | 2017-09-15 |
| Date Completed: | 2017-09-18 |
| Next Due Date: | 2018-09-17 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

| | |
|----------------|---|
| Description | : 'SVANTEK' Integrating Sound Level Meter |
| Manufacturer | : SVANTEK |
| Model No. | : SVAN 955 |
| Serial No. | : 12553 |
| Microphone No. | : 35222 |
| Equipment No. | : N-08-02 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 22 degree Celsius |
| Relative Humidity | : 60% |

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

| Reference Set Point, dB | Instrument Readings, dB |
|-------------------------|-------------------------|
| 94 | 94.0 |
| 114 | 114.0 |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|-------------|
| Test Report No.: | C/N/170915A |
| Date of Issue: | 2017-09-18 |
| Date Received: | 2017-09-15 |
| Date Tested: | 2017-09-15 |
| Date Completed: | 2017-09-18 |
| Next Due Date: | 2018-09-17 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

| | |
|----------------|---|
| Description | : 'SVANTEK' Integrating Sound Level Meter |
| Manufacturer | : SVANTEK |
| Model No. | : SVAN 955 |
| Serial No. | : 12563 |
| Microphone No. | : 34377 |
| Equipment No. | : N-08-03 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 22 degree Celsius |
| Relative Humidity | : 60% |

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

| Reference Set Point, dB | Instrument Readings, dB |
|-------------------------|-------------------------|
| 94 | 94.0 |
| 114 | 114.0 |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/N/170825 |
| Date of Issue: | 2017-08-28 |
| Date Received: | 2017-08-25 |
| Date Tested: | 2017-08-25 |
| Date Completed: | 2017-08-28 |
| Next Due Date: | 2018-08-27 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

| | |
|----------------|---|
| Description | : 'SVANTEK' Integrating Sound Level Meter |
| Manufacturer | : SVANTEK |
| Model No. | : SVAN 957 |
| Serial No. | : 21455 |
| Microphone No. | : 43730 |
| Equipment No. | : N-08-07 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 23 degree Celsius |
| Relative Humidity | : 60 % |

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

| Reference Set Point, dB | Instrument Readings, dB |
|-------------------------|-------------------------|
| 94 | 94.0 |
| 114 | 114.0 |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/N/170818 |
| Date of Issue: | 2017-08-21 |
| Date Received: | 2017-08-18 |
| Date Tested: | 2017-08-18 |
| Date Completed: | 2017-08-21 |
| Next Due Date: | 2018-08-20 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

| | |
|----------------|---|
| Description | : 'SVANTEK' Integrating Sound Level Meter |
| Manufacturer | : SVANTEK |
| Model No. | : SVAN 957 |
| Serial No. | : 21459 |
| Microphone No. | : 43676 |
| Equipment No. | : N-08-08 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 22 degree Celsius |
| Relative Humidity | : 61 % |

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

| Reference Set Point, dB | Instrument Readings, dB |
|-------------------------|-------------------------|
| 94 | 94.0 |
| 114 | 114.0 |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|-------------|
| Test Report No.: | C/N/170818A |
| Date of Issue: | 2017-08-21 |
| Date Received: | 2017-08-18 |
| Date Tested: | 2017-08-18 |
| Date Completed: | 2017-08-21 |
| Next Due Date: | 2018-08-20 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

| | |
|----------------|---|
| Description | : 'SVANTEK' Integrating Sound Level Meter |
| Manufacturer | : SVANTEK |
| Model No. | : SVAN 957 |
| Serial No. | : 21460 |
| Microphone No. | : 43679 |
| Equipment No. | : N-08-09 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 22 degree Celsius |
| Relative Humidity | : 61 % |

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

| Reference Set Point, dB | Instrument Readings, dB |
|-------------------------|-------------------------|
| 94 | 94.0 |
| 114 | 114.0 |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|-------------|
| Test Report No.: | C/N/170915C |
| Date of Issue: | 2017-09-18 |
| Date Received: | 2017-09-15 |
| Date Tested: | 2017-09-15 |
| Date Completed: | 2017-09-18 |
| Next Due Date: | 2018-09-17 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

| | |
|----------------|---|
| Description | : 'SVANTEK' Integrating Sound Level Meter |
| Manufacturer | : SVANTEK |
| Model No. | : SVAN 977 |
| Serial No. | : 45482 |
| Microphone No. | : 63626 |
| Equipment No. | : N-08-14 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 22 degree Celsius |
| Relative Humidity | : 60% |

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

| Reference Set Point, dB | Instrument Readings, dB |
|-------------------------|-------------------------|
| 94 | 94.0 |
| 114 | 114.0 |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|--------------|
| Test Report No.: | C/N/161028/1 |
| Date of Issue: | 2016-10-31 |
| Date Received: | 2016-10-28 |
| Date Tested: | 2016-10-28 |
| Date Completed: | 2016-10-31 |
| Next Due Date: | 2017-10-30 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Item for calibration:

| | |
|---------------|-------------------------|
| Description | : Acoustical Calibrator |
| Manufacturer | : SVANTEK |
| Model No. | : SV30A |
| Serial No. | : 10965 |
| Equipment No. | : N-09-02 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 21 degree Celsius |
| Relative Humidity | : 60 % |

Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

| Sound Pressure Level (1kHz) | Measured SPL | Tolerance |
|-----------------------------|--------------|----------------|
| At 94 dB SPL | 94.0 | 94.0 ± 0.1 dB |
| At 114 dB SPL | 114.0 | 114.0 ± 0.1 dB |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE

Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/N/170929 |
| Date of Issue: | 2017-09-30 |
| Date Received: | 2017-09-29 |
| Date Tested: | 2017-09-29 |
| Date Completed: | 2017-09-30 |
| Next Due Date: | 2018-09-29 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Item for calibration:

| | |
|---------------|-------------------------|
| Description | : Acoustical Calibrator |
| Manufacturer | : SVANTEK |
| Model No. | : SV30A |
| Serial No. | : 24803 |
| Equipment No. | : N-09-03 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 21 degree Celsius |
| Relative Humidity | : 60 % |

Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

| Sound Pressure Level (1kHz) | Measured SPL | Tolerance |
|-----------------------------|--------------|----------------|
| At 94 dB SPL | 94.0 | 94.0 ± 0.1 dB |
| At 114 dB SPL | 114.0 | 114.0 ± 0.1 dB |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|-------------|
| Test Report No.: | C/N/170929B |
| Date of Issue: | 2017-09-30 |
| Date Received: | 2017-09-29 |
| Date Tested: | 2017-09-29 |
| Date Completed: | 2017-09-30 |
| Next Due Date: | 2018-09-29 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Item for calibration:

| | |
|---------------|-------------------------|
| Description | : Acoustical Calibrator |
| Manufacturer | : SVANTEK |
| Model No. | : SV30A |
| Serial No. | : 24780 |
| Equipment No. | : N-09-05 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 21 degree Celsius |
| Relative Humidity | : 60 % |

Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

| Sound Pressure Level (1kHz) | Measured SPL | Tolerance |
|-----------------------------|--------------|----------------|
| At 94 dB SPL | 94.0 | 94.0 ± 0.1 dB |
| At 114 dB SPL | 114.0 | 114.0 ± 0.1 dB |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|--------------|
| Test Report No.: | C/N/161104/1 |
| Date of Issue: | 2016-11-07 |
| Date Received: | 2016-11-04 |
| Date Tested: | 2016-11-04 |
| Date Completed: | 2016-11-07 |
| Next Due Date: | 2017-11-06 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Item for calibration:

| | |
|---------------|-------------------------|
| Description | : Acoustical Calibrator |
| Manufacturer | : Brüel & Kjær |
| Model No. | : 4231 |
| Serial No. | : 2326353 |
| Equipment No. | : N-02-01 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 21 degree Celsius |
| Relative Humidity | : 62 % |

Methodology:

The sound calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

| Sound Pressure Level (1kHz) | Measured SPL | Tolerance |
|-----------------------------|--------------|----------------|
| At 94 dB SPL | 94.0 | 94.0 ± 0.1 dB |
| At 114 dB SPL | 114.0 | 114.0 ± 0.1 dB |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|-------------|
| Test Report No.: | C/N/170818C |
| Date of Issue: | 2017-08-21 |
| Date Received: | 2017-08-18 |
| Date Tested: | 2017-08-18 |
| Date Completed: | 2017-08-21 |
| Next Due Date: | 2018-08-20 |

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

| | |
|---------------|-------------------------|
| Description | : Acoustical Calibrator |
| Manufacturer | : Brüel & Kjær |
| Model No. | : 4231 |
| Serial No. | : 2412367 |
| Equipment No. | : N-02-03 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 22 degree Celsius |
| Relative Humidity | : 61 % |

Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

| Sound Pressure Level (1kHz) | Measured SPL | Tolerance |
|-----------------------------|--------------|----------------|
| At 94 dB SPL | 94.0 | 94.0 ± 0.1 dB |
| At 114 dB SPL | 114.0 | 114.0 ± 0.1 dB |

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE

Laboratory Manager

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA16034/08/0007

Station: AM1 - Tin Hau Temple Operator: MH
 Date: 8-Sep-17 Next Due Date: 7-Nov-17
 Equipment No.: A-01-05 Serial No. 10599

| Ambient Condition | | | |
|---------------------|-------|---------------------|-----|
| Temperature, Ta (K) | 301.6 | Pressure, Pa (mmHg) | 760 |

| Orifice Transfer Standard Information | | | | | |
|---------------------------------------|-----------|--|--------|---------------|----------|
| Serial No.: | 0993 | Slope, mc (CFM) | 0.0578 | Intercept, bc | -0.04890 |
| Last Calibration Date: | 28-Feb-17 | $mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | | | |
| Next Calibration Date: | 27-Feb-18 | $Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$ | | | |

| Calibration of TSP Sampler | | | | | |
|----------------------------|------------------------------------|--|---------------------|--------------------------------|---|
| Calibration Point | Orifice | | | HVS | |
| | ΔH (orifice), in. of water | $[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | Qstd (CFM) X - axis | ΔW (HVS), in. of water | $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis |
| 1 | 13.3 | 3.63 | 63.59 | 6.8 | 2.59 |
| 2 | 9.9 | 3.13 | 54.98 | 5.2 | 2.27 |
| 3 | 8.7 | 2.93 | 51.60 | 4.5 | 2.11 |
| 4 | 5.4 | 2.31 | 40.83 | 3.1 | 1.75 |
| 5 | 3.2 | 1.78 | 31.62 | 1.9 | 1.37 |

By Linear Regression of Y on X

Slope, mw = 0.0378 Intercept, bw : 0.1838
 Correlation coefficient* = 0.9993

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM
 From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W = $(mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 3.31

Remarks: _____

Conducted by: hes Signature: hes
 Checked by: lav Signature: _____

Date: 8/9/17
 Date: 8 September 2017

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA16034/08/0007

Station: AM2 - Sai Tso Wan Recreation Ground Operator: MH
 Date: 8-Sep-17 Next Due Date: 7-Nov-17
 Equipment No.: A-01-08 Serial No. 1287

| Ambient Condition | | | |
|---------------------|-------|---------------------|-------|
| Temperature, Ta (K) | 301.2 | Pressure, Pa (mmHg) | 759.7 |

| Orifice Transfer Standard Information | | | | | |
|---------------------------------------|-----------|--|--------|---------------|----------|
| Serial No.: | 0993 | Slope, mc (CFM) | 0.0578 | Intercept, bc | -0.04890 |
| Last Calibration Date: | 28-Feb-17 | $mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | | | |
| Next Calibration Date: | 27-Feb-18 | $Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$ | | | |

| Calibration of TSP Sampler | | | | | |
|----------------------------|------------------------------------|--|------------------------|--------------------------------|--|
| Calibration Point | Orifice | | | HVS | |
| | ΔH (orifice), in. of water | $[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | Qstd (CFM) X - axis | ΔW (HVS), in. of water | $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis |
| 1 | 13.2 | 3.61 | 63.39 | 7.9 | 2.80 |
| 2 | 10.7 | 3.25 | 57.15 | 6.2 | 2.48 |
| 3 | 8.6 | 2.92 | 51.33 | 5.3 | 2.29 |
| 4 | 5.3 | 2.29 | 40.47 | 3.1 | 1.75 |
| 5 | 3.2 | 1.78 | 31.64 | 2.0 | 1.41 |

By Linear Regression of Y on X

Slope, mw = 0.0438 Intercept, bw : 0.0078
 Correlation coefficient* = 0.9986

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W = $(mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 3.61

Remarks: _____

Conducted by: hei Signature: hei Date: 8/9/17
 Checked by: lv Signature: _____ Date: 8 September 2017

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA16034/03/0006

Station: AM3 - Yau Lai Estate, Bik Lai House Operator: MH
 Date: 4-Sep-17 Next Due Date: 3-Nov-17
 Equipment No.: A-01-03 Serial No. 10379

| Ambient Condition | | | |
|---------------------|-------|---------------------|-------|
| Temperature, Ta (K) | 300.5 | Pressure, Pa (mmHg) | 757.4 |

| Orifice Transfer Standard Information | | | | | |
|---------------------------------------|-----------|--|--------|---------------|----------|
| Serial No.: | 0993 | Slope, mc (CFM) | 0.0578 | Intercept, bc | -0.04890 |
| Last Calibration Date: | 28-Feb-17 | $mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | | | |
| Next Calibration Date: | 27-Feb-18 | $Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$ | | | |

| Calibration of TSP Sampler | | | | | |
|----------------------------|------------------------------------|--|---------------------|--------------------------------|---|
| Calibration Point | Orifice | | | HVS | |
| | ΔH (orifice), in. of water | $[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | Qstd (CFM) X - axis | ΔW (HVS), in. of water | $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis |
| 1 | 12.8 | 3.56 | 62.41 | 7.4 | 2.70 |
| 2 | 10.4 | 3.21 | 56.34 | 6.0 | 2.44 |
| 3 | 7.2 | 2.67 | 47.02 | 4.3 | 2.06 |
| 4 | 5.2 | 2.27 | 40.09 | 3.2 | 1.78 |
| 5 | 3.3 | 1.81 | 32.11 | 2.1 | 1.44 |

By Linear Regression of Y on X

Slope, mw = 0.0414 Intercept, bw = 0.1136
 Correlation coefficient* = 0.9999

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM
 From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W = $(mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 3.63

Remarks: _____

Conducted by: hs Signature: hs Date: 4/9/17
 Checked by: hs Signature: _____ Date: 4 September 2017

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA16034/54/0007

Station: AM4(A) - Cha Kwo Ling Public Cargo Working Area Administrative Office Operator: MH

Date: 13-Sep-17 Next Due Date: 12-Nov-17

Equipment No.: A-01-54 Serial No. 1536

| Ambient Condition | | | |
|---------------------|-------|---------------------|-------|
| Temperature, Ta (K) | 302.6 | Pressure, Pa (mmHg) | 760.9 |

| Orifice Transfer Standard Information | | | | | |
|---------------------------------------|-----------|--|--------|---------------|----------|
| Serial No.: | 0993 | Slope, mc (CFM) | 0.0578 | Intercept, bc | -0.04890 |
| Last Calibration Date: | 28-Feb-17 | $mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | | | |
| Next Calibration Date: | 27-Feb-18 | $Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$ | | | |

| Calibration of TSP Sampler | | | | | |
|----------------------------|------------------------------------|--|-------------------|--------------------------------|---|
| Calibration Point | Orifice | | | HVS | |
| | ΔH (orifice), in. of water | $[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | Qstd (CFM) X-axis | ΔW (HVS), in. of water | $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis |
| 1 | 17.5 | 4.15 | 72.75 | 10.6 | 3.23 |
| 2 | 13.6 | 3.66 | 64.23 | 8.2 | 2.84 |
| 3 | 10.4 | 3.20 | 56.27 | 6.7 | 2.57 |
| 4 | 6.8 | 2.59 | 45.67 | 4.3 | 2.06 |
| 5 | 4.1 | 2.01 | 35.65 | 3.0 | 1.72 |

By Linear Regression of Y on X

Slope, mw = 0.0411 Intercept, bw = 0.2289

Correlation coefficient* = 0.9985

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W = $(mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 4.04

Remarks: _____

Conducted by: ker Signature: ker Date: 13/9/17

Checked by: ku Signature: _____ Date: 13 September 2017

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA16034/37/0007

Station: AM5(A) - DSD Desilting Compound Operator: MH
 Date: 8-Sep-17 Next Due Date: 7-Nov-17
 Equipment No.: A-01-37 Serial No. 1704

| Ambient Condition | | | |
|---------------------|-------|---------------------|-------|
| Temperature, Ta (K) | 302.3 | Pressure, Pa (mmHg) | 759.4 |

| Orifice Transfer Standard Information | | | | | |
|---------------------------------------|-----------|--|--------|---------------|----------|
| Serial No.: | 0993 | Slope, mc (CFM) | 0.0578 | Intercept, bc | -0.04890 |
| Last Calibration Date: | 28-Feb-17 | $mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | | | |
| Next Calibration Date: | 27-Feb-18 | $Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$ | | | |

| Calibration of TSP Sampler | | | | | |
|----------------------------|------------------------------------|--|---------------------|--------------------------------|---|
| Calibration Point | Orifice | | | HVS | |
| | ΔH (orifice), in. of water | $[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | Qstd (CFM) X - axis | ΔW (HVS), in. of water | $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis |
| 1 | 17.4 | 4.14 | 72.50 | 8.8 | 2.94 |
| 2 | 13.8 | 3.69 | 64.66 | 7.1 | 2.64 |
| 3 | 10.8 | 3.26 | 57.30 | 5.8 | 2.39 |
| 4 | 6.8 | 2.59 | 45.64 | 3.4 | 1.83 |
| 5 | 4.3 | 2.06 | 36.47 | 2.3 | 1.51 |

By Linear Regression of Y on X

Slope, mw = 0.0407 Intercept, bw = 0.0120
 Correlation coefficient* = 0.9985

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM
 From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W = $(mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 3.15

Remarks: _____

Conducted by: her Signature: her Date: 8/9/17
 Checked by: LA Signature: _____ Date: 8 September 2017

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA16034/07/0007

Station AM6 - Park Central Operator: WK
 Date: 29-Sep-17 Next Due Date: 28-Nov-17
 Equipment No.: A-01-07 Serial No.: 10592

| Ambient Condition | | | |
|---------------------|-------|---------------------|-------|
| Temperature, Ta (K) | 302.8 | Pressure, Pa (mmHg) | 762.5 |

| Orifice Transfer Standard Information | | | | | |
|---------------------------------------|-----------|--|--------|---------------|----------|
| Serial No. | 0993 | Slope, mc | 0.0578 | Intercept, bc | -0.04890 |
| Last Calibration Date: | 28-Feb-17 | $mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | | | |
| Next Calibration Date: | 27-Feb-18 | $Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$ | | | |

| Calibration of TSP Sampler | | | | | |
|----------------------------|------------------------------------|--|-------------------|--------------------------------|---|
| Calibration Point | Orifice | | | HVS | |
| | ΔH (orifice), in. of water | $[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$ | Qstd (CFM) X-axis | ΔW (HVS), in. of water | $[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis |
| 1 | 11.8 | 3.41 | 59.93 | 7.4 | 2.70 |
| 2 | 9.7 | 3.09 | 54.41 | 6.2 | 2.47 |
| 3 | 7.5 | 2.72 | 47.95 | 4.8 | 2.18 |
| 4 | 5.4 | 2.31 | 40.81 | 3.3 | 1.81 |
| 5 | 3.6 | 1.89 | 33.48 | 2.4 | 1.54 |

By Linear Regression of Y on X

Slope, mw = 0.0451 Intercept, bw = 0.0078
 Correlation coefficient* = 0.9986

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 3.83

Remarks: _____

Conducted by: Wk Tang Signature: [Signature]
 Checked by: [Signature] Signature: _____

Date: 29/9/17
 Date: 29 September 2017



TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE
 VILLAGE OF CLEVELS, OH
 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Feb 28, 2017 Rootsmeter S/N 0438320 Ta (K) - 294
 Operator Tisch Orifice I.D. - 0993 Pa (mm) - 750.57

| PLATE OR Run # | VOLUME START (m3) | VOLUME STOP (m3) | DIFF VOLUME (m3) | DIFF TIME (min) | METER | ORFICE |
|----------------------|-------------------------|------------------------|------------------------|-----------------------|--------------------|----------------------|
| | | | | | DIFF Hg (mm) | DIFF H2O (in.) |
| 1 | NA | NA | 1.00 | 1.3860 | 3.2 | 2.00 |
| 2 | NA | NA | 1.00 | 0.9910 | 6.4 | 4.00 |
| 3 | NA | NA | 1.00 | 0.8840 | 7.9 | 5.00 |
| 4 | NA | NA | 1.00 | 0.8430 | 8.7 | 5.50 |
| 5 | NA | NA | 1.00 | 0.6970 | 12.6 | 8.00 |

DATA TABULATION

| Vstd | (x axis) Qstd | (y axis) | Va | (x axis) Qa | (y axis) |
|-------------------------------------|------------------|----------|---------------------------|----------------|----------|
| 0.9967 | 0.7191 | 1.4149 | 0.9957 | 0.7184 | 0.8851 |
| 0.9925 | 1.0015 | 2.0010 | 0.9915 | 1.0005 | 1.2517 |
| 0.9904 | 1.1204 | 2.2372 | 0.9894 | 1.1192 | 1.3995 |
| 0.9894 | 1.1737 | 2.3464 | 0.9884 | 1.1725 | 1.4678 |
| 0.9842 | 1.4120 | 2.8299 | 0.9832 | 1.4106 | 1.7702 |
| Qstd slope (m) = 2.04055 | | | Qa slope (m) = 1.27776 | | |
| intercept (b) = -0.04890 | | | intercept (b) = -0.03059 | | |
| coefficient (r) = 0.99995 | | | coefficient (r) = 0.99995 | | |
| y axis = SQRT[H2O(Pa/760) (298/Ta)] | | | y axis = SQRT[H2O(Ta/Pa)] | | |

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)
 Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]
 Qa = Va/Time

For subsequent flow rate calculations:

Qstd = 1/m{ [SQRT(H2O(Pa/760) (298/Ta))] - b}
 Qa = 1/m{ [SQRT H2O(Ta/Pa)] - b}

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

| | |
|------------------|------------|
| Test Report No.: | C/170818 |
| Date of Issue: | 2017-08-21 |
| Date Received: | 2017-08-18 |
| Date Tested: | 2017-08-18 |
| Date Completed: | 2017-08-21 |
| Next Due Date: | 2018-02-20 |

ATTN: Miss Mei Ling Tang

Page: 1 of 2

Certificate of Calibration

Item for calibration:

| | |
|--------------|----------------------|
| Description | : Weather Monitor II |
| Manufacturer | : Davis Instruments |
| Model No. | : 7440 |
| Serial No. | : MC01010A44 |

Test conditions:

| | |
|-------------------|---------------------|
| Room Temperature | : 22 degree Celsius |
| Relative Humidity | : 64 % |

Test Specifications:


1. Performance check of anemometer
2. Performance check of wind direction sensor

Methodology:

In-house method with reference anemometer (RS232 Integral Vane Digital Anemometer)

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

| | |
|------------------|------------|
| Test Report No.: | C/170818 |
| Date of Issue: | 2017-08-21 |
| Date Received: | 2017-08-18 |
| Date Tested: | 2017-08-18 |
| Date Completed: | 2017-08-21 |
| Next Due Date: | 2018-02-20 |
| Page: | 2 of 2 |

Results:

1. Performance check of anemometer

| Air Velocity, m/s | | Difference D (m/s) |
|-------------------------|----------------------|--------------------|
| Instrument Reading (V1) | Reference Value (V1) | D = V1 - V2 |
| 2.00 | 2.00 | 0.00 |

2. Performance check of wind direction sensor

| Wind Direction (°) | | Difference D (°) |
|-------------------------|----------------------|------------------|
| Instrument Reading (W1) | Reference Value (W2) | D = W1 - W2 |
| 0 | 0 | 0 |
| 45 | 45 | 0 |
| 90.2 | 90 | 0.2 |
| 135 | 135 | 0 |
| 180.1 | 180 | 0.1 |
| 224.9 | 225 | -0.1 |
| 270 | 270 | 0 |
| 315.1 | 315 | 0.1 |
| 360 | 360 | 0 |

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|------------------|-------------|
| Test Report No.: | C/W/170826A |
| Date of Issue: | 2017-08-26 |
| Date Received: | 2017-08-26 |
| Date Tested: | 2017-08-26 |
| Date Completed: | 2017-08-26 |
| Next Due Date: | 2017-11-25 |

ATTN: Miss Mei Ling Tang

Page: 1 of 2

Certificate of Calibration

Item for calibration:

| | | |
|---|---------------------------------|------------------------------|
| YSI EXO1 Multiparameter Sondes | Equipment No.: | SW-08-09 (S/N: 16J100869) |
| Manufacturer: | YSI Incorporated, a Xylem brand | |
| Description: | Model No. | Serial No. |
| - EXO Optical DO Sensor, Ti | 599100-01 | 16H102988 |
| - EXO conductivity/Temperature Sensor, Ti | 599870 | 16G102310 |
| - EXO Turbidity Sensor, Ti | 599101-01 | 16H102467 |
| - EXO pH Sensor Assembly, Guarded, Ti | 599701 | 16J100419 |

Test conditions:

Room Temperature : 21 degree Celsius
Relative Humidity : 65%

Test Specifications:

Performance checking for Conductivity, Temperature, pH, Dissolved oxygen (D.O.) and Turbidity

Methodology:

According to manufacturer instruction manual, APHA 20e 4500-O C

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

| | |
|------------------|-------------|
| Test Report No.: | C/W/170826A |
| Date of Issue: | 2017-08-26 |
| Date Received: | 2017-08-26 |
| Date Tested: | 2017-08-26 |
| Date Completed: | 2017-08-26 |
| Next Due Date: | 2017-11-25 |

Page: 2 of 2

Certificate of Calibration

Results:

Conductivity performance checking

| | Instrument Readings ($\mu\text{S}/\text{cm}$) | Acceptance Criteria | Comment |
|--|---|---------------------|---------|
| KCl stock solution (12890 $\mu\text{S}/\text{cm}$) | 13000 | 12246-13534 | Pass |

Temperature performance checking

| Reference thermometer- E431 Readings ($^{\circ}\text{C}$) | Instrument Readings ($^{\circ}\text{C}$) | Correction ($^{\circ}\text{C}$) | Comment |
|--|--|-----------------------------------|---------|
| 22.4 | 22.407 | -0.007 | N/A |

pH performance checking

| | Instrument Readings (pH unit) | Acceptance Criteria | Comment |
|-------------------|----------------------------------|---------------------|---------|
| pH QC buffer 4.00 | 4.01 | 4.00 ± 0.10 | Pass |
| pH QC buffer 6.86 | 6.87 | 6.86 ± 0.10 | Pass |
| pH QC buffer 9.18 | 9.20 | 9.18 ± 0.10 | Pass |

D.O. performance checking

| | Instrument Readings (mg/L) | Acceptance Criteria | Comment |
|------------------|----------------------------|--------------------------|---------|
| Zero DO solution | 0.05 | $<0.1\text{mg}/\text{L}$ | Pass |

| Winkler Titration value (mg/L) | Instrument Readings (mg/L) | Acceptance Criteria | Comment |
|-----------------------------------|----------------------------|---|---------|
| 8.00 | 7.86 | Difference between Titration value and instrument reading $<0.2\text{mg}/\text{L}$ | Pass |

Turbidity performance checking

| Turbidity stock solution | Instrument Readings (NTU) | Acceptance Criteria | Comment |
|--------------------------|---------------------------|---------------------|---------|
| 10 NTU | 10.23 | 9.0-11.0 | Pass |
| 50 NTU | 51.03 | 45.0-55.0 | Pass |
| 100 NTU | 101.5 | 90.0-110.0 | Pass |

Depth performance checking

| Water Depth | Instrument Readings (NTU) | Acceptance Criteria | Comment |
|-------------|---------------------------|---------------------|---------|
| 0.5 meter | 0.50 | 0.45-0.55 | Pass |

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|------------------|-------------|
| Test Report No.: | C/W/170826C |
| Date of Issue: | 2017-08-26 |
| Date Received: | 2017-08-26 |
| Date Tested: | 2017-08-26 |
| Date Completed: | 2017-08-26 |
| Next Due Date: | 2017-11-25 |

ATTN: Miss Mei Ling Tang

Page: 1 of 2

Certificate of Calibration

Item for calibration:

| | | | |
|---|---------------------------------|------------------------------|--|
| YSI EXO1 Multiparameter Sondes | Equipment No.: | SW-08-61 (S/N: 16J102333) | |
| Manufacturer: | YSI Incorporated, a Xylem brand | | |
| Description: | Model No. | Serial No. | |
| - EXO Optical DO Sensor, Ti | 599100-01 | 16J100986 | |
| - EXO conductivity/Temperature Sensor, Ti | 599870 | 16H100170 | |
| - EXO Turbidity Sensor, Ti | 599101-01 | 16J101140 | |
| - EXO pH Sensor Assembly, Guarded, Ti | 599701 | 16J101307 | |

Test conditions:

Room Temperature : 21 degree Celsius
Relative Humidity : 65%

Test Specifications:

Performance checking for Conductivity, Temperature, pH, Dissolved oxygen (D.O.) and Turbidity

Methodology:

According to manufacturer instruction manual, APHA 20e 4500-O C

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

| | |
|------------------|-------------|
| Test Report No.: | C/W/170826C |
| Date of Issue: | 2017-08-26 |
| Date Received: | 2017-08-26 |
| Date Tested: | 2017-08-26 |
| Date Completed: | 2017-08-26 |
| Next Due Date: | 2017-11-25 |
| Page: | 2 of 2 |

Certificate of Calibration

Results:

Conductivity performance checking

| | Instrument Readings ($\mu\text{S}/\text{cm}$) | Acceptance Criteria | Comment |
|--|---|---------------------|---------|
| KCl stock solution (12890 $\mu\text{S}/\text{cm}$) | 12900 | 12246-13534 | Pass |

Temperature performance checking

| Reference thermometer- E431 Readings ($^{\circ}\text{C}$) | Instrument Readings ($^{\circ}\text{C}$) | Correction ($^{\circ}\text{C}$) | Comment |
|--|--|-----------------------------------|---------|
| 22.4 | 22.406 | -0.006 | N/A |

pH performance checking

| | Instrument Readings (pH unit) | Acceptance Criteria | Comment |
|-------------------|----------------------------------|---------------------|---------|
| pH QC buffer 4.00 | 4.01 | 4.00 ± 0.10 | Pass |
| pH QC buffer 6.86 | 6.87 | 6.86 ± 0.10 | Pass |
| pH QC buffer 9.18 | 9.19 | 9.18 ± 0.10 | Pass |

D.O. performance checking

| | Instrument Readings (mg/L) | Acceptance Criteria | Comment |
|------------------|----------------------------|--------------------------|---------|
| Zero DO solution | 0.05 | $<0.1\text{mg}/\text{L}$ | Pass |

| Winkler Titration value (mg/L) | Instrument Readings (mg/L) | Acceptance Criteria | Comment |
|-----------------------------------|----------------------------|---|---------|
| 8.00 | 7.96 | Difference between Titration value and instrument reading $<0.2\text{mg}/\text{L}$ | Pass |

Turbidity performance checking

| Turbidity stock solution | Instrument Readings (NTU) | Acceptance Criteria | Comment |
|--------------------------|---------------------------|---------------------|---------|
| 10 NTU | 10.36 | 9.0-11.0 | Pass |
| 50 NTU | 50.13 | 45.0-55.0 | Pass |
| 100 NTU | 102.4 | 90.0-110.0 | Pass |

Depth performance checking

| Water Depth | Instrument Readings (NTU) | Acceptance Criteria | Comment |
|-------------|---------------------------|---------------------|---------|
| 0.5 meter | 0.50 | 0.45-0.55 | Pass |

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|------------------|-------------|
| Test Report No.: | C/W/170826D |
| Date of Issue: | 2017-08-26 |
| Date Received: | 2017-08-26 |
| Date Tested: | 2017-08-26 |
| Date Completed: | 2017-08-26 |
| Next Due Date: | 2017-11-25 |

ATTN: Miss Mei Ling Tang

Page: 1 of 2

Certificate of Calibration

Item for calibration:

| | | |
|---|---------------------------------|------------------------------|
| YSI EXO1 Multiparameter Sondes | Equipment No.: | SW-08-85 (S/N: 17B100180) |
| Manufacturer: | YSI Incorporated, a Xylem brand | |
| Description: | Model No. | Serial No. |
| - EXO Optical DO Sensor, Ti | 599100-01 | 17A105009 |
| - EXO conductivity/Temperature Sensor, Ti | 599870 | 17A105103 |
| - EXO Turbidity Sensor, Ti | 599101-01 | 17A104092 |
| - EXO pH Sensor Assembly, Guarded, Ti | 599701 | 17A105263 |

Test conditions:

Room Temperature : 21 degree Celsius
Relative Humidity : 65%

Test Specifications:

Performance checking for Conductivity, Temperature, pH, Dissolved oxygen (D.O.) and Turbidity

Methodology:

According to manufacturer instruction manual, APHA 20e 4500-O C

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

| | |
|------------------|-------------|
| Test Report No.: | C/W/170826D |
| Date of Issue: | 2017-08-26 |
| Date Received: | 2017-08-26 |
| Date Tested: | 2017-08-26 |
| Date Completed: | 2017-08-26 |
| Next Due Date: | 2017-11-25 |

Page: 2 of 2

Certificate of Calibration

Results:

Conductivity performance checking

| | Instrument Readings ($\mu\text{S/cm}$) | Acceptance Criteria | Comment |
|---|--|---------------------|---------|
| KCl stock solution (12890 $\mu\text{S/cm}$) | 12900 | 12246-13534 | Pass |

Temperature performance checking

| Reference thermometer- E431 Readings ($^{\circ}\text{C}$) | Instrument Readings ($^{\circ}\text{C}$) | Correction ($^{\circ}\text{C}$) | Comment |
|--|--|-----------------------------------|---------|
| 22.4 | 22.408 | -0.008 | N/A |

pH performance checking

| | Instrument Readings (pH unit) | Acceptance Criteria | Comment |
|-------------------|----------------------------------|---------------------|---------|
| pH QC buffer 4.00 | 4.01 | 4.00 ± 0.10 | Pass |
| pH QC buffer 6.86 | 6.88 | 6.86 ± 0.10 | Pass |
| pH QC buffer 9.18 | 9.19 | 9.18 ± 0.10 | Pass |

D.O. performance checking

| | Instrument Readings (mg/L) | Acceptance Criteria | Comment |
|------------------|----------------------------|---------------------|---------|
| Zero DO solution | 0.05 | $<0.1\text{mg/L}$ | Pass |

| Winkler Titration value (mg/L) | Instrument Readings (mg/L) | Acceptance Criteria | Comment |
|-----------------------------------|----------------------------|--|---------|
| 8.00 | 7.99 | Difference between Titration value and instrument reading $<0.2\text{mg/L}$ | Pass |

Turbidity performance checking

| Turbidity stock solution | Instrument Readings (NTU) | Acceptance Criteria | Comment |
|--------------------------|---------------------------|---------------------|---------|
| 10 NTU | 10.04 | 9.0-11.0 | Pass |
| 50 NTU | 50.27 | 45.0-55.0 | Pass |
| 100 NTU | 101.8 | 90.0-110.0 | Pass |

Depth performance checking

| Water Depth | Instrument Readings (NTU) | Acceptance Criteria | Comment |
|-------------|---------------------------|---------------------|---------|
| 0.5 meter | 0.50 | 0.45-0.55 | Pass |

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|------------------|-------------|
| Test Report No.: | C/W/170826E |
| Date of Issue: | 2017-08-26 |
| Date Received: | 2017-08-26 |
| Date Tested: | 2017-08-26 |
| Date Completed: | 2017-08-26 |
| Next Due Date: | 2017-11-25 |

ATTN: Miss Mei Ling Tang

Page: 1 of 2

Certificate of Calibration

Item for calibration:

| | | | |
|---|---------------------------------|-------------------------------|--|
| YSI EXO1 Multiparameter Sondes | Equipment No.: | SW-08-107 (S/N: 17B100680) | |
| Manufacturer: | YSI Incorporated, a Xylem brand | | |
| Description: | Model No. | Serial No. | |
| - EXO Optical DO Sensor, Ti | 599100-01 | 17B101535 | |
| - EXO conductivity/Temperature Sensor, Ti | 599870 | 17B100782 | |
| - EXO Turbidity Sensor, Ti | 599101-01 | 17B101578 | |
| - EXO pH Sensor Assembly, Guarded, Ti | 599701 | 17B103614 | |

Test conditions:

Room Temperature : 21 degree Celsius
Relative Humidity : 65%

Test Specifications:

Performance checking for Conductivity, Temperature, pH, Dissolved oxygen (D.O.) and Turbidity

Methodology:

According to manufacturer instruction manual, APHA 20e 4500-O C

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

| | |
|------------------|-------------|
| Test Report No.: | C/W/170826E |
| Date of Issue: | 2017-08-26 |
| Date Received: | 2017-08-26 |
| Date Tested: | 2017-08-26 |
| Date Completed: | 2017-08-26 |
| Next Due Date: | 2017-11-25 |

Page: 2 of 2

Certificate of Calibration

Results:

Conductivity performance checking

| | Instrument Readings ($\mu\text{S}/\text{cm}$) | Acceptance Criteria | Comment |
|--|---|---------------------|---------|
| KCl stock solution (12890 $\mu\text{S}/\text{cm}$) | 13000 | 12246-13534 | Pass |

Temperature performance checking

| Reference thermometer- E43 I Readings ($^{\circ}\text{C}$) | Instrument Readings ($^{\circ}\text{C}$) | Correction ($^{\circ}\text{C}$) | Comment |
|---|--|-----------------------------------|---------|
| 22.4 | 22.421 | -0.021 | N/A |

pH performance checking

| | Instrument Readings (pH unit) | Acceptance Criteria | Comment |
|-------------------|----------------------------------|---------------------|---------|
| pH QC buffer 4.00 | 4.01 | 4.00 ± 0.10 | Pass |
| pH QC buffer 6.86 | 6.87 | 6.86 ± 0.10 | Pass |
| pH QC buffer 9.18 | 9.22 | 9.18 ± 0.10 | Pass |

D.O. performance checking

| | Instrument Readings (mg/L) | Acceptance Criteria | Comment |
|------------------|----------------------------|--------------------------|---------|
| Zero DO solution | 0.05 | $<0.1\text{mg}/\text{L}$ | Pass |

| Winkler Titration value (mg/L) | Instrument Readings (mg/L) | Acceptance Criteria | Comment |
|-----------------------------------|----------------------------|---|---------|
| 8.00 | 8.11 | Difference between Titration value and instrument reading $<0.2\text{mg}/\text{L}$ | Pass |

Turbidity performance checking

| | Instrument Readings (NTU) | Acceptance Criteria | Comment |
|------------------------------------|---------------------------|---------------------|---------|
| Turbidity stock solution 10 NTU | 10.09 | 9.0-11.0 | Pass |
| 50 NTU | 50.52 | 45.0-55.0 | Pass |
| 100 NTU | 101.2 | 90.0-110.0 | Pass |

Depth performance checking

| Water Depth | Instrument Readings (NTU) | Acceptance Criteria | Comment |
|-------------|---------------------------|---------------------|---------|
| 0.5 meter | 0.50 | 0.45-0.55 | Pass |

*****END OF REPORT*****

CALIBRATION CERTIFICATE


Calibration Item: Minimate Plus Unit (Calibration with Geophone
BG16959)
Model No.: 716A0403
Serial No.: BE17506
Calibration Date: 11 April 2017
Next Calibration Date: 11 April 2018
Method Used: In-house Method B3-001
In-house Testing Procedure No.: B3-001

| <u>Test References</u> | <u>Model</u> | <u>Serial No.</u> |
|--------------------------------------|--------------|-------------------|
| Blastmate III | 714A0801 | BA15521 |
| ISEE Triaxial Geophone | 714A9701 | BG14463 |
| GLOBAL SPECIALISTS 3MHz* | 2030 | 256812 |
| Stanford Spectrum Analyzer | SR760 | 41550 |
| Aglient Multimeter* | 34410A | MY47011119 |
| HP Distortion Meter* | 339A | 810699 |
| Bruel & Kjaer Accelerometer* | 4370 | 30323 |
| Bruel & Kjaer Charge Amplifier* | 2647 | 2518810 |
| Bruel & Kjaer Conditional Amplifier* | 269 | 2152173 |
| LDS Air Cooled Vibrator | V556 | 92794/1 |
| LDS Field Power Supply | FPS10L | ARA 04/05 |
| LDS Power Amplifier | PA1000L | ARA 07/06 |

*References are traceable to NIST or equivalent.

INSTANTEL INC. hereby certifies that this unit has been calibrated and that the results are consistent with the specifications published regarding this instrument. The SENSORCHECK feature of the unit is sufficiently reliable to indicate proper operation, although it is recommended that this unit be sent to INSTANTEL or an authorized service center for regular calibration.

Authorized by: _____


(Au Yeung Hang Chuen, Isaac)

Date: 11 April 2017

CALIBRATION CERTIFICATE

Calibration Item: TRIAXIAL GEOPHONE (Calibration with main unit BE17506)
Part Number: 714A9701
Serial No.: BG16959
Calibration Date: 11 April 2017
Next Calibration Date: 11 April 2018
Method Used: In-house Method B3-001
In-house Testing Procedure No.: B3-001

| <u>Test References</u> | <u>Model</u> | <u>Serial No.</u> |
|--------------------------------------|--------------|-------------------|
| Blastmate III | 714A0801 | BA15521 |
| ISEE Triaxial Geophone | 714A9701 | BG14463 |
| GLOBAL SPECIALISTS 3MHz* | 2030 | 256812 |
| Stanford Spectrum Analyzer | SR760 | 41550 |
| Aglient Multimeter* | 34410A | MY47011119 |
| HP Distortion Meter* | 339A | 810699 |
| Bruel & Kjaer Accelerometer* | 4370 | 30323 |
| Bruel & Kjaer Charge Amplifier* | 2647 | 2518810 |
| Bruel & Kjaer Conditional Amplifier* | 269 | 2152173 |
| LDS Air Cooled Vibrator | V556 | 92794/1 |
| LDS Field Power Supply | FPS10L | ARA 04/05 |
| LDS Power Amplifier | PA1000L | ARA 07/06 |

*References are traceable to NIST or equivalent.

INSTANTEL INC. hereby certifies that this unit has been calibrated and that the results are consistent with the specifications published regarding this instrument. The SENSORCHECK feature of the unit is sufficiently reliable to indicate proper operation, although it is recommended that this unit be sent to INSTANTEL or an authorized service center for regular calibration.

Authorized by: _____

(Au Yeung Hang Chuen, Isaac)

Date: 11 April 2017

- when it has to be **right**



Leica Geosystems Calibration Certificate **Blue**

Calibration Certificate Blue without measurement values issued by Authorised Service Centre

| | | | |
|----------------------|--|------------------------|--|
| Product | DNA03 digital level | Certificate No. | 347062-18012017 |
| Article No. | 723289 | Inspection Date | 18.01.2017 |
| Serial No. | 347062 | Order No. | 501047397 |
| Equipment No. | 5937807 | PO No. | PO |
| Issued by | Authorised Service Centre Leica Geosystems Ltd. Kowloon, Hong Kong Hongkong | Ordered by | LEIGHTON - CHINA STATE J.V. HONG KONG Hongkong |
| | | Customer | LEIGHTON - CHINA STATE J.V. HONG KONG Hongkong |

Compliance

The Calibration Certificate Blue without measurement values issued by Authorised Service Centre corresponds to the Producer Inspection Certificate O in accordance with DIN 55 350 Part 18-4.2.1.

Certificate

We hereby certify that the product described has been tested and complies with the specifications of the product. The test equipment used is traceable to national standards or to recognized procedures. This is established by our Quality Management System, audited and certified to ISO 9001 by an independent national accredited certification body.




Leica Geosystems Ltd.

18.01.2017




Stella Kam
Operations Manager


Jacky Ng
Service Manager

Certificate No. 347062-18012017

Article No. 5003367

This Certificate may not be reproduced other than in full except with prior written approval of the issuing authority.

Leica Geosystems AG
Heinrich-Wild-Strasse
9435 Heerbrugg
Switzerland
Telephone +41 71 / 727 31 31
www.leica-geosystems.com



Calibration Certificate

Number: CCP/66453

Customer Name: Far East Metal & Hardware Company
Contact Person: Ms. Cherry Yiu
Detector Model: Crowcon Tetra Portable Gas Detector
Serial Number: 100486262/01-020

| Sensor Type | Measuring Range | Alarm Level Settings | | | | Test Gas | Result |
|-------------|-----------------|----------------------|---------|------|------|----------|--------|
| | | Alarm 1 | Alarm 2 | STEL | LTEL | | |
| CH4 | 0 to 100%LEL | 20 | 40 | NA | NA | 50%LEL | Passed |
| H2S | 0 to 100ppm | 5 | 10 | 10 | 5 | 25ppm | Passed |
| O2 | 0 to 25%v/v | 19.0 | 23.5 | NA | NA | 18.0%v/v | Passed |
| CO | 0 to 500ppm | 30 | 100 | 200 | 30 | 100ppm | Passed |

Next Calibration Date: 5th January 2018

Remarks:

1. "Passed" refers to the detector has been successfully calibrated to meet with manufacturer tolerance of the instrument & sensor specification and repeatability $\pm 5\%$ FSD.
2. The above equipment has been tested and calibrated in accordance with procedures referred to in Crowcon's BSI validated ISO9001 quality manual. Test equipment used has been factory calibrated and is traceable to national standards. Canned calibration gas has been prepared in accordance with BS4559 and original gas mixture has been prepared using NPL (UK) certified Gravimetric Standard. Gas generator has been tested to meet with: Mil Std 45662A / ANSI/NCSL Z540-1

Mark Chan

Technical Service Manager

6th January 2017



FireMark Hong Kong Limited
Flat A, 11/F., Hop Hing Industrial Building, 704 Castle Peak Road, Lai Chi Kok,
Kowloon, Hong Kong.
Tel : (852) 2751 8871 Fax : (852) 2751 880

**APPENDIX C
WEATHER INFORMATION**

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

I. General Information

| Date | Mean Air Temperature (°C) | Mean Relative Humidity (%) | Precipitation (mm) |
|-----------------|----------------------------------|-----------------------------------|---------------------------|
| 1 October 2017 | 26.4 - 32.7 | 86 | 6.6 |
| 2 October 2017 | 28.3 - 33.5 | 83 | 3.6 |
| 3 October 2017 | 27.5 – 31.0 | 78 | 0 |
| 4 October 2017 | 27.5 - 30.3 | 82 | 9.5 |
| 5 October 2017 | 27.4 - 31.1 | 76 | Trace |
| 6 October 2017 | 27.9 - 31.7 | 75 | 0.2 |
| 7 October 2017 | 27.3 - 31.5 | 74 | 0 |
| 8 October 2017 | 28.1 - 30.9 | 75 | 0 |
| 9 October 2017 | 28.6 - 32.3 | 71 | Trace |
| 10 October 2017 | 28.3 - 32.5 | 74 | Trace |
| 11 October 2017 | 27.6 - 32.7 | 73 | 0.2 |
| 12 October 2017 | 24.5 - 30.6 | 69 | 0 |
| 13 October 2017 | 21.9 - 25.6 | 64 | 0 |
| 14 October 2017 | 20.4 - 26.9 | 68 | 0.4 |
| 15 October 2017 | 25.6 - 27.5 | 89 | 20.7 |
| 16 October 2017 | 24.7 - 27.6 | 91 | 17.1 |
| 17 October 2017 | 24.0 - 29.5 | 87 | 41.3 |
| 18 October 2017 | 23.4 - 27.9 | 74 | Trace |
| 19 October 2017 | 22.3 - 27.8 | 71 | 0 |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

I. General Information

| Date | Mean Air Temperature (°C) | Mean Relative Humidity (%) | Precipitation (mm) |
|-----------------|----------------------------------|-----------------------------------|---------------------------|
| 20 October 2017 | 21.6 - 27.2 | 69 | 0 |
| 21 October 2017 | 20.2 - 26.3 | 64 | 0 |
| 22 October 2017 | 20.8 - 27.7 | 60 | 0 |
| 23 October 2017 | 22.5 - 27.3 | 62 | 0 |
| 24 October 2017 | 22.7 - 26.4 | 65 | 0 |
| 25 October 2017 | 22.1 - 28.1 | 69 | Trace |
| 26 October 2017 | 22.1 - 28.6 | 71 | 0 |
| 27 October 2017 | 22.5 - 28.0 | 60 | 0 |
| 28 October 2017 | 21.7 - 27.0 | 54 | 0 |
| 29 October 2017 | 20.5 - 25.0 | 53 | 0 |
| 30 October 2017 | 19.0 - 25.0 | 55 | Trace |
| 31 October 2017 | 26.4 - 32.7 | 61 | Trace |

* The above information was extracted from the daily weather summary by Hong Kong Observatory.

** Trace means rainfall less than 0.05 mm

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| Date | Time | Wind Speed m/s | Direction |
|-------------|-------------|-----------------------|------------------|
| 1-Oct-2017 | 0:00 | 1.8 | E |
| 1-Oct-2017 | 1:00 | 1.7 | N |
| 1-Oct-2017 | 2:00 | 1.5 | NNE |
| 1-Oct-2017 | 3:00 | 1.7 | E |
| 1-Oct-2017 | 4:00 | 1.2 | E |
| 1-Oct-2017 | 5:00 | 1.3 | WNW |
| 1-Oct-2017 | 6:00 | 1 | SE |
| 1-Oct-2017 | 7:00 | 1.3 | SSE |
| 1-Oct-2017 | 8:00 | 1.4 | S |
| 1-Oct-2017 | 9:00 | 1.7 | SSE |
| 1-Oct-2017 | 10:00 | 2.2 | N |
| 1-Oct-2017 | 11:00 | 2.3 | ESE |
| 1-Oct-2017 | 12:00 | 2.3 | NNE |
| 1-Oct-2017 | 13:00 | 2.4 | ESE |
| 1-Oct-2017 | 14:00 | 2 | E |
| 1-Oct-2017 | 15:00 | 2 | ENE |
| 1-Oct-2017 | 16:00 | 1.6 | NE |
| 1-Oct-2017 | 17:00 | 1.5 | ESE |
| 1-Oct-2017 | 18:00 | 1.6 | SE |
| 1-Oct-2017 | 19:00 | 1.4 | ENE |
| 1-Oct-2017 | 20:00 | 1.3 | SSE |
| 1-Oct-2017 | 21:00 | 2 | NE |
| 1-Oct-2017 | 22:00 | 2 | WNW |
| 1-Oct-2017 | 23:00 | 1.7 | ESE |
| 2-Oct-2017 | 0:00 | 1.3 | SSE |
| 2-Oct-2017 | 1:00 | 1.1 | NW |
| 2-Oct-2017 | 2:00 | 1.3 | NW |
| 2-Oct-2017 | 3:00 | 1.1 | S |
| 2-Oct-2017 | 4:00 | 1.1 | NE |
| 2-Oct-2017 | 5:00 | 1.1 | NNE |
| 2-Oct-2017 | 6:00 | 1 | NE |
| 2-Oct-2017 | 7:00 | 1.1 | ENE |
| 2-Oct-2017 | 8:00 | 1.3 | ENE |
| 2-Oct-2017 | 9:00 | 1.4 | WNW |
| 2-Oct-2017 | 10:00 | 1.6 | WNW |
| 2-Oct-2017 | 11:00 | 1.6 | WSW |
| 2-Oct-2017 | 12:00 | 2 | WSW |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|------------|-------|-----|-----|
| 2-Oct-2017 | 13:00 | 2 | WSW |
| 2-Oct-2017 | 14:00 | 2.1 | SW |
| 2-Oct-2017 | 15:00 | 2 | NE |
| 2-Oct-2017 | 16:00 | 1.7 | SW |
| 2-Oct-2017 | 17:00 | 1.7 | SW |
| 2-Oct-2017 | 18:00 | 1.5 | ENE |
| 2-Oct-2017 | 19:00 | 1.3 | ENE |
| 2-Oct-2017 | 20:00 | 1.1 | ENE |
| 2-Oct-2017 | 21:00 | 1.3 | SSW |
| 2-Oct-2017 | 22:00 | 1.2 | SSE |
| 2-Oct-2017 | 23:00 | 1.2 | WSW |
| 3-Oct-2017 | 0:00 | 1.4 | NNE |
| 3-Oct-2017 | 1:00 | 1.4 | NNE |
| 3-Oct-2017 | 2:00 | 1.4 | W |
| 3-Oct-2017 | 3:00 | 1.4 | SSW |
| 3-Oct-2017 | 4:00 | 1.3 | N |
| 3-Oct-2017 | 5:00 | 1.3 | N |
| 3-Oct-2017 | 6:00 | 1 | ENE |
| 3-Oct-2017 | 7:00 | 1.1 | NNE |
| 3-Oct-2017 | 8:00 | 1 | ESE |
| 3-Oct-2017 | 9:00 | 1.5 | SE |
| 3-Oct-2017 | 10:00 | 1.8 | ENE |
| 3-Oct-2017 | 11:00 | 1.7 | SE |
| 3-Oct-2017 | 12:00 | 1.8 | E |
| 3-Oct-2017 | 13:00 | 2.3 | NE |
| 3-Oct-2017 | 14:00 | 1.8 | ESE |
| 3-Oct-2017 | 15:00 | 1.3 | ESE |
| 3-Oct-2017 | 16:00 | 1.8 | ESE |
| 3-Oct-2017 | 17:00 | 1.6 | SE |
| 3-Oct-2017 | 18:00 | 1.5 | SE |
| 3-Oct-2017 | 19:00 | 1.1 | SW |
| 3-Oct-2017 | 20:00 | 1 | WSW |
| 3-Oct-2017 | 21:00 | 0.9 | NE |
| 3-Oct-2017 | 22:00 | 1.1 | SSW |
| 3-Oct-2017 | 23:00 | 1.1 | S |
| 4-Oct-2017 | 0:00 | 0.9 | S |
| 4-Oct-2017 | 1:00 | 1 | WSW |
| 4-Oct-2017 | 2:00 | 1 | W |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|------------|-------|-----|-----|
| 4-Oct-2017 | 3:00 | 1.1 | N |
| 4-Oct-2017 | 4:00 | 1.2 | W |
| 4-Oct-2017 | 5:00 | 1 | NE |
| 4-Oct-2017 | 6:00 | 1.2 | NE |
| 4-Oct-2017 | 7:00 | 1.1 | ENE |
| 4-Oct-2017 | 8:00 | 1.3 | NNE |
| 4-Oct-2017 | 9:00 | 1.7 | ESE |
| 4-Oct-2017 | 10:00 | 2 | ESE |
| 4-Oct-2017 | 11:00 | 2.1 | ENE |
| 4-Oct-2017 | 12:00 | 2.1 | SSE |
| 4-Oct-2017 | 13:00 | 2.2 | SE |
| 4-Oct-2017 | 14:00 | 2 | SSE |
| 4-Oct-2017 | 15:00 | 2 | ESE |
| 4-Oct-2017 | 16:00 | 1.9 | SE |
| 4-Oct-2017 | 17:00 | 2.3 | SSE |
| 4-Oct-2017 | 18:00 | 2 | SSE |
| 4-Oct-2017 | 19:00 | 1.8 | SSE |
| 4-Oct-2017 | 20:00 | 1.7 | SSE |
| 4-Oct-2017 | 21:00 | 1.4 | NE |
| 4-Oct-2017 | 22:00 | 1.7 | NE |
| 4-Oct-2017 | 23:00 | 1.5 | SE |
| 5-Oct-2017 | 0:00 | 1.4 | SE |
| 5-Oct-2017 | 1:00 | 1.4 | SSE |
| 5-Oct-2017 | 2:00 | 1.1 | SSE |
| 5-Oct-2017 | 3:00 | 1.3 | ESE |
| 5-Oct-2017 | 4:00 | 1.6 | SSE |
| 5-Oct-2017 | 5:00 | 1.7 | NNE |
| 5-Oct-2017 | 6:00 | 1.4 | ESE |
| 5-Oct-2017 | 7:00 | 1.2 | SSW |
| 5-Oct-2017 | 8:00 | 1.6 | W |
| 5-Oct-2017 | 9:00 | 1.9 | W |
| 5-Oct-2017 | 10:00 | 2 | WNW |
| 5-Oct-2017 | 11:00 | 2 | SSW |
| 5-Oct-2017 | 12:00 | 1.8 | ENE |
| 5-Oct-2017 | 13:00 | 1.9 | NNE |
| 5-Oct-2017 | 14:00 | 2 | W |
| 5-Oct-2017 | 15:00 | 2.5 | SW |
| 5-Oct-2017 | 16:00 | 2.6 | WNW |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|------------|-------|-----|-----|
| 5-Oct-2017 | 17:00 | 2.3 | WNW |
| 5-Oct-2017 | 18:00 | 2.1 | SW |
| 5-Oct-2017 | 19:00 | 1.7 | SSE |
| 5-Oct-2017 | 20:00 | 1.7 | NE |
| 5-Oct-2017 | 21:00 | 1.6 | W |
| 5-Oct-2017 | 22:00 | 1.6 | S |
| 5-Oct-2017 | 23:00 | 1.6 | NNW |
| 6-Oct-2017 | 0:00 | 1.4 | NW |
| 6-Oct-2017 | 1:00 | 1.3 | NNW |
| 6-Oct-2017 | 2:00 | 1.3 | SSE |
| 6-Oct-2017 | 3:00 | 1.4 | SE |
| 6-Oct-2017 | 4:00 | 1.4 | SSE |
| 6-Oct-2017 | 5:00 | 1.4 | SE |
| 6-Oct-2017 | 6:00 | 1.4 | SE |
| 6-Oct-2017 | 7:00 | 1.3 | SE |
| 6-Oct-2017 | 8:00 | 1.3 | WNW |
| 6-Oct-2017 | 9:00 | 1.5 | WNW |
| 6-Oct-2017 | 10:00 | 1.8 | WNW |
| 6-Oct-2017 | 11:00 | 2.1 | W |
| 6-Oct-2017 | 12:00 | 2.3 | WSW |
| 6-Oct-2017 | 13:00 | 2.2 | SSE |
| 6-Oct-2017 | 14:00 | 2.3 | WNW |
| 6-Oct-2017 | 15:00 | 2.1 | WNW |
| 6-Oct-2017 | 16:00 | 2 | SW |
| 6-Oct-2017 | 17:00 | 1.8 | ENE |
| 6-Oct-2017 | 18:00 | 1.7 | NNE |
| 6-Oct-2017 | 19:00 | 1.4 | NNE |
| 6-Oct-2017 | 20:00 | 1.3 | NE |
| 6-Oct-2017 | 21:00 | 1 | NNE |
| 6-Oct-2017 | 22:00 | 0.9 | NE |
| 6-Oct-2017 | 23:00 | 0.8 | ENE |
| 7-Oct-2017 | 0:00 | 0.9 | NE |
| 7-Oct-2017 | 1:00 | 1 | SE |
| 7-Oct-2017 | 2:00 | 0.8 | E |
| 7-Oct-2017 | 3:00 | 0.8 | NE |
| 7-Oct-2017 | 4:00 | 0.8 | NW |
| 7-Oct-2017 | 5:00 | 0.8 | N |
| 7-Oct-2017 | 6:00 | 1.1 | NE |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|------------|-------|-----|-----|
| 7-Oct-2017 | 7:00 | 1.2 | NNE |
| 7-Oct-2017 | 8:00 | 1.1 | ENE |
| 7-Oct-2017 | 9:00 | 1.3 | SSE |
| 7-Oct-2017 | 10:00 | 1.6 | SSE |
| 7-Oct-2017 | 11:00 | 1.8 | NE |
| 7-Oct-2017 | 12:00 | 2 | N |
| 7-Oct-2017 | 13:00 | 1.5 | NE |
| 7-Oct-2017 | 14:00 | 1.5 | N |
| 7-Oct-2017 | 15:00 | 1.5 | NE |
| 7-Oct-2017 | 16:00 | 1.2 | NE |
| 7-Oct-2017 | 17:00 | 1.2 | E |
| 7-Oct-2017 | 18:00 | 1.1 | E |
| 7-Oct-2017 | 19:00 | 0.9 | E |
| 7-Oct-2017 | 20:00 | 0.8 | NW |
| 7-Oct-2017 | 21:00 | 0.7 | NE |
| 7-Oct-2017 | 22:00 | 0.8 | E |
| 7-Oct-2017 | 23:00 | 0.9 | SSW |
| 8-Oct-2017 | 0:00 | 0.9 | SW |
| 8-Oct-2017 | 1:00 | 1 | SSW |
| 8-Oct-2017 | 2:00 | 1.1 | SSE |
| 8-Oct-2017 | 3:00 | 0.9 | SW |
| 8-Oct-2017 | 4:00 | 1 | NNE |
| 8-Oct-2017 | 5:00 | 1 | WNW |
| 8-Oct-2017 | 6:00 | 1.1 | WSW |
| 8-Oct-2017 | 7:00 | 1.1 | SSW |
| 8-Oct-2017 | 8:00 | 1.3 | W |
| 8-Oct-2017 | 9:00 | 1.5 | NNE |
| 8-Oct-2017 | 10:00 | 2 | ENE |
| 8-Oct-2017 | 11:00 | 2.1 | ESE |
| 8-Oct-2017 | 12:00 | 2.3 | E |
| 8-Oct-2017 | 13:00 | 2.3 | ENE |
| 8-Oct-2017 | 14:00 | 2.2 | SSE |
| 8-Oct-2017 | 15:00 | 2.4 | ENE |
| 8-Oct-2017 | 16:00 | 2.4 | ENE |
| 8-Oct-2017 | 17:00 | 2.2 | ESE |
| 8-Oct-2017 | 18:00 | 1.8 | ESE |
| 8-Oct-2017 | 19:00 | 1.7 | ESE |
| 8-Oct-2017 | 20:00 | 1.4 | ESE |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 8-Oct-2017 | 21:00 | 1.5 | SSE |
| 8-Oct-2017 | 22:00 | 1.5 | SE |
| 8-Oct-2017 | 23:00 | 1.4 | ENE |
| 9-Oct-2017 | 0:00 | 1.3 | W |
| 9-Oct-2017 | 1:00 | 1.1 | E |
| 9-Oct-2017 | 2:00 | 1 | S |
| 9-Oct-2017 | 3:00 | 1.4 | NE |
| 9-Oct-2017 | 4:00 | 1.4 | WNW |
| 9-Oct-2017 | 5:00 | 1 | N |
| 9-Oct-2017 | 6:00 | 1 | W |
| 9-Oct-2017 | 7:00 | 0.8 | ENE |
| 9-Oct-2017 | 8:00 | 1 | N |
| 9-Oct-2017 | 9:00 | 1 | W |
| 9-Oct-2017 | 10:00 | 1.5 | N |
| 9-Oct-2017 | 11:00 | 1.6 | NNE |
| 9-Oct-2017 | 12:00 | 1.8 | N |
| 9-Oct-2017 | 13:00 | 1.8 | WSW |
| 9-Oct-2017 | 14:00 | 1.8 | WNW |
| 9-Oct-2017 | 15:00 | 1.8 | NE |
| 9-Oct-2017 | 16:00 | 1.8 | ENE |
| 9-Oct-2017 | 17:00 | 1.6 | NE |
| 9-Oct-2017 | 18:00 | 1.2 | SE |
| 9-Oct-2017 | 19:00 | 1 | ENE |
| 9-Oct-2017 | 20:00 | 1.2 | SSW |
| 9-Oct-2017 | 21:00 | 1.1 | N |
| 9-Oct-2017 | 22:00 | 1.1 | ENE |
| 9-Oct-2017 | 23:00 | 1 | SSE |
| 10-Oct-2017 | 0:00 | 1.1 | SSE |
| 10-Oct-2017 | 1:00 | 1.3 | NE |
| 10-Oct-2017 | 2:00 | 1.1 | NE |
| 10-Oct-2017 | 3:00 | 0.9 | SE |
| 10-Oct-2017 | 4:00 | 0.9 | W |
| 10-Oct-2017 | 5:00 | 0.9 | NW |
| 10-Oct-2017 | 6:00 | 0.8 | SSW |
| 10-Oct-2017 | 7:00 | 0.9 | ENE |
| 10-Oct-2017 | 8:00 | 1.1 | SSW |
| 10-Oct-2017 | 9:00 | 1.5 | W |
| 10-Oct-2017 | 10:00 | 1.9 | WNW |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 10-Oct-2017 | 11:00 | 2 | W |
| 10-Oct-2017 | 12:00 | 1.9 | WSW |
| 10-Oct-2017 | 13:00 | 2 | SW |
| 10-Oct-2017 | 14:00 | 1.9 | W |
| 10-Oct-2017 | 15:00 | 1.5 | NNE |
| 10-Oct-2017 | 16:00 | 1.7 | SW |
| 10-Oct-2017 | 17:00 | 1.7 | SW |
| 10-Oct-2017 | 18:00 | 1.4 | WNW |
| 10-Oct-2017 | 19:00 | 0.9 | SSW |
| 10-Oct-2017 | 20:00 | 1.1 | SW |
| 10-Oct-2017 | 21:00 | 1.2 | S |
| 10-Oct-2017 | 22:00 | 1.1 | SW |
| 10-Oct-2017 | 23:00 | 1.1 | WNW |
| 11-Oct-2017 | 0:00 | 1.2 | SW |
| 11-Oct-2017 | 1:00 | 1.3 | WNW |
| 11-Oct-2017 | 2:00 | 1.3 | WSW |
| 11-Oct-2017 | 3:00 | 1.3 | N |
| 11-Oct-2017 | 4:00 | 1.2 | N |
| 11-Oct-2017 | 5:00 | 1 | E |
| 11-Oct-2017 | 6:00 | 0.9 | NW |
| 11-Oct-2017 | 7:00 | 0.9 | WNW |
| 11-Oct-2017 | 8:00 | 0.9 | N |
| 11-Oct-2017 | 9:00 | 1.2 | WNW |
| 11-Oct-2017 | 10:00 | 1.5 | W |
| 11-Oct-2017 | 11:00 | 1.5 | WNW |
| 11-Oct-2017 | 12:00 | 1.7 | NNE |
| 11-Oct-2017 | 13:00 | 1.7 | SE |
| 11-Oct-2017 | 14:00 | 1.6 | SSW |
| 11-Oct-2017 | 15:00 | 1.6 | NNE |
| 11-Oct-2017 | 16:00 | 1.5 | ENE |
| 11-Oct-2017 | 17:00 | 1.3 | NE |
| 11-Oct-2017 | 18:00 | 1.2 | S |
| 11-Oct-2017 | 19:00 | 1 | ENE |
| 11-Oct-2017 | 20:00 | 1 | N |
| 11-Oct-2017 | 21:00 | 0.9 | ENE |
| 11-Oct-2017 | 22:00 | 0.9 | NE |
| 11-Oct-2017 | 23:00 | 1 | ENE |
| 12-Oct-2017 | 0:00 | 1 | SSW |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 12-Oct-2017 | 1:00 | 0.9 | NNE |
| 12-Oct-2017 | 2:00 | 1 | W |
| 12-Oct-2017 | 3:00 | 1 | NNE |
| 12-Oct-2017 | 4:00 | 0.9 | NNE |
| 12-Oct-2017 | 5:00 | 1.1 | NNE |
| 12-Oct-2017 | 6:00 | 1.1 | NE |
| 12-Oct-2017 | 7:00 | 0.9 | NE |
| 12-Oct-2017 | 8:00 | 1 | ESE |
| 12-Oct-2017 | 9:00 | 1.3 | ENE |
| 12-Oct-2017 | 10:00 | 1.7 | NE |
| 12-Oct-2017 | 11:00 | 1.9 | ESE |
| 12-Oct-2017 | 12:00 | 2 | NNE |
| 12-Oct-2017 | 13:00 | 2.2 | SW |
| 12-Oct-2017 | 14:00 | 2.3 | WNW |
| 12-Oct-2017 | 15:00 | 2.6 | NE |
| 12-Oct-2017 | 16:00 | 2.3 | NE |
| 12-Oct-2017 | 17:00 | 2.3 | NE |
| 12-Oct-2017 | 18:00 | 2.1 | NE |
| 12-Oct-2017 | 19:00 | 1.8 | NNE |
| 12-Oct-2017 | 20:00 | 1.6 | NE |
| 12-Oct-2017 | 21:00 | 1.5 | NNE |
| 12-Oct-2017 | 22:00 | 1.6 | NNE |
| 12-Oct-2017 | 23:00 | 1.9 | NNE |
| 13-Oct-2017 | 0:00 | 1.4 | NNE |
| 13-Oct-2017 | 1:00 | 1.6 | NNE |
| 13-Oct-2017 | 2:00 | 1.4 | NNE |
| 13-Oct-2017 | 3:00 | 1.3 | NNE |
| 13-Oct-2017 | 4:00 | 1.1 | NE |
| 13-Oct-2017 | 5:00 | 1.2 | SSE |
| 13-Oct-2017 | 6:00 | 1.1 | ESE |
| 13-Oct-2017 | 7:00 | 1 | NNE |
| 13-Oct-2017 | 8:00 | 1.2 | NNE |
| 13-Oct-2017 | 9:00 | 1.6 | NNE |
| 13-Oct-2017 | 10:00 | 1.6 | ENE |
| 13-Oct-2017 | 11:00 | 1.9 | ENE |
| 13-Oct-2017 | 12:00 | 2.1 | WNW |
| 13-Oct-2017 | 13:00 | 2 | SSE |
| 13-Oct-2017 | 14:00 | 2 | NE |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 13-Oct-2017 | 15:00 | 2 | NNE |
| 13-Oct-2017 | 16:00 | 1.9 | N |
| 13-Oct-2017 | 17:00 | 1.6 | NE |
| 13-Oct-2017 | 18:00 | 1.5 | ESE |
| 13-Oct-2017 | 19:00 | 1.6 | SE |
| 13-Oct-2017 | 20:00 | 1.4 | E |
| 13-Oct-2017 | 21:00 | 1.5 | ESE |
| 13-Oct-2017 | 22:00 | 1.2 | ENE |
| 13-Oct-2017 | 23:00 | 1.4 | NNE |
| 14-Oct-2017 | 0:00 | 1.2 | NNE |
| 14-Oct-2017 | 1:00 | 1.2 | NNE |
| 14-Oct-2017 | 2:00 | 1.2 | ENE |
| 14-Oct-2017 | 3:00 | 1.2 | SSE |
| 14-Oct-2017 | 4:00 | 1.2 | W |
| 14-Oct-2017 | 5:00 | 1.1 | NNW |
| 14-Oct-2017 | 6:00 | 1.1 | WSW |
| 14-Oct-2017 | 7:00 | 1 | NE |
| 14-Oct-2017 | 8:00 | 1.1 | NNE |
| 14-Oct-2017 | 9:00 | 1.4 | SSE |
| 14-Oct-2017 | 10:00 | 1.5 | SSE |
| 14-Oct-2017 | 11:00 | 2 | SSE |
| 14-Oct-2017 | 12:00 | 2.1 | ENE |
| 14-Oct-2017 | 13:00 | 2 | NNE |
| 14-Oct-2017 | 14:00 | 1.8 | W |
| 14-Oct-2017 | 15:00 | 1.7 | W |
| 14-Oct-2017 | 16:00 | 1.9 | WSW |
| 14-Oct-2017 | 17:00 | 1.8 | N |
| 14-Oct-2017 | 18:00 | 1.6 | ENE |
| 14-Oct-2017 | 19:00 | 1.5 | ESE |
| 14-Oct-2017 | 20:00 | 1.6 | S |
| 14-Oct-2017 | 21:00 | 1.8 | SW |
| 14-Oct-2017 | 22:00 | 1.9 | WSW |
| 14-Oct-2017 | 23:00 | 1.4 | WSW |
| 15-Oct-2017 | 0:00 | 1.7 | WSW |
| 15-Oct-2017 | 1:00 | 1.4 | ESE |
| 15-Oct-2017 | 2:00 | 1.8 | NE |
| 15-Oct-2017 | 3:00 | 1.5 | ENE |
| 15-Oct-2017 | 4:00 | 1.6 | SSE |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 15-Oct-2017 | 5:00 | 1.5 | ENE |
| 15-Oct-2017 | 6:00 | 1.6 | NNE |
| 15-Oct-2017 | 7:00 | 1.4 | ENE |
| 15-Oct-2017 | 8:00 | 1.4 | NNE |
| 15-Oct-2017 | 9:00 | 1.5 | ENE |
| 15-Oct-2017 | 10:00 | 1.7 | NE |
| 15-Oct-2017 | 11:00 | 1.7 | ENE |
| 15-Oct-2017 | 12:00 | 1.9 | ENE |
| 15-Oct-2017 | 13:00 | 1.9 | ENE |
| 15-Oct-2017 | 14:00 | 1.8 | ESE |
| 15-Oct-2017 | 15:00 | 1.7 | NNE |
| 15-Oct-2017 | 16:00 | 1.6 | NNE |
| 15-Oct-2017 | 17:00 | 1.6 | NE |
| 15-Oct-2017 | 18:00 | 1.4 | E |
| 15-Oct-2017 | 19:00 | 1.1 | NNE |
| 15-Oct-2017 | 20:00 | 1 | NE |
| 15-Oct-2017 | 21:00 | 1 | NNE |
| 15-Oct-2017 | 22:00 | 0.9 | ENE |
| 15-Oct-2017 | 23:00 | 1 | ENE |
| 16-Oct-2017 | 0:00 | 1 | ENE |
| 16-Oct-2017 | 1:00 | 1 | ENE |
| 16-Oct-2017 | 2:00 | 1.1 | NE |
| 16-Oct-2017 | 3:00 | 1.1 | NE |
| 16-Oct-2017 | 4:00 | 1.2 | NE |
| 16-Oct-2017 | 5:00 | 1.2 | NE |
| 16-Oct-2017 | 6:00 | 1.1 | NE |
| 16-Oct-2017 | 7:00 | 1.3 | ENE |
| 16-Oct-2017 | 8:00 | 1.4 | NNE |
| 16-Oct-2017 | 9:00 | 1.7 | NE |
| 16-Oct-2017 | 10:00 | 1.7 | NE |
| 16-Oct-2017 | 11:00 | 1.7 | WNW |
| 16-Oct-2017 | 12:00 | 2 | ENE |
| 16-Oct-2017 | 13:00 | 2 | ENE |
| 16-Oct-2017 | 14:00 | 1.9 | ENE |
| 16-Oct-2017 | 15:00 | 2 | ESE |
| 16-Oct-2017 | 16:00 | 1.9 | NE |
| 16-Oct-2017 | 17:00 | 1.6 | ENE |
| 16-Oct-2017 | 18:00 | 1.2 | NNE |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 16-Oct-2017 | 19:00 | 1.2 | SW |
| 16-Oct-2017 | 20:00 | 0.9 | SSW |
| 16-Oct-2017 | 21:00 | 0.9 | ENE |
| 16-Oct-2017 | 22:00 | 1.2 | N |
| 16-Oct-2017 | 23:00 | 1 | E |
| 17-Oct-2017 | 0:00 | 1.3 | ENE |
| 17-Oct-2017 | 1:00 | 1.5 | ENE |
| 17-Oct-2017 | 2:00 | 1.7 | N |
| 17-Oct-2017 | 3:00 | 1.5 | ESE |
| 17-Oct-2017 | 4:00 | 1.3 | NE |
| 17-Oct-2017 | 5:00 | 1.2 | NE |
| 17-Oct-2017 | 6:00 | 1.3 | NE |
| 17-Oct-2017 | 7:00 | 1.5 | NNE |
| 17-Oct-2017 | 8:00 | 1.7 | NNE |
| 17-Oct-2017 | 9:00 | 2 | NNE |
| 17-Oct-2017 | 10:00 | 2 | NE |
| 17-Oct-2017 | 11:00 | 1.7 | E |
| 17-Oct-2017 | 12:00 | 1.9 | N |
| 17-Oct-2017 | 13:00 | 2 | NNE |
| 17-Oct-2017 | 14:00 | 2.1 | E |
| 17-Oct-2017 | 15:00 | 2.3 | NNE |
| 17-Oct-2017 | 16:00 | 2.4 | ENE |
| 17-Oct-2017 | 17:00 | 2.1 | SE |
| 17-Oct-2017 | 18:00 | 1.7 | ESE |
| 17-Oct-2017 | 19:00 | 1.5 | ESE |
| 17-Oct-2017 | 20:00 | 1.6 | NE |
| 17-Oct-2017 | 21:00 | 1.4 | NE |
| 17-Oct-2017 | 22:00 | 1.6 | S |
| 17-Oct-2017 | 23:00 | 1.4 | W |
| 18-Oct-2017 | 0:00 | 1.3 | W |
| 18-Oct-2017 | 1:00 | 1.4 | NNE |
| 18-Oct-2017 | 2:00 | 1.3 | NE |
| 18-Oct-2017 | 3:00 | 1.6 | NW |
| 18-Oct-2017 | 4:00 | 1.9 | S |
| 18-Oct-2017 | 5:00 | 1.8 | NE |
| 18-Oct-2017 | 6:00 | 1.8 | ENE |
| 18-Oct-2017 | 7:00 | 1.6 | SE |
| 18-Oct-2017 | 8:00 | 1.9 | ESE |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 18-Oct-2017 | 9:00 | 1.6 | SSE |
| 18-Oct-2017 | 10:00 | 1.8 | SSW |
| 18-Oct-2017 | 11:00 | 2.1 | NNE |
| 18-Oct-2017 | 12:00 | 2.2 | NNE |
| 18-Oct-2017 | 13:00 | 2.3 | NE |
| 18-Oct-2017 | 14:00 | 2.5 | ESE |
| 18-Oct-2017 | 15:00 | 2.6 | ESE |
| 18-Oct-2017 | 16:00 | 2.6 | NE |
| 18-Oct-2017 | 17:00 | 2.1 | NE |
| 18-Oct-2017 | 18:00 | 1.8 | W |
| 18-Oct-2017 | 19:00 | 1.5 | NE |
| 18-Oct-2017 | 20:00 | 1.3 | NE |
| 18-Oct-2017 | 21:00 | 1.4 | NW |
| 18-Oct-2017 | 22:00 | 1.4 | NNE |
| 18-Oct-2017 | 23:00 | 2 | NNE |
| 19-Oct-2017 | 0:00 | 1.9 | NNE |
| 19-Oct-2017 | 1:00 | 2 | WNW |
| 19-Oct-2017 | 2:00 | 1.8 | WNW |
| 19-Oct-2017 | 3:00 | 1.7 | WNW |
| 19-Oct-2017 | 4:00 | 1.8 | N |
| 19-Oct-2017 | 5:00 | 1.6 | SW |
| 19-Oct-2017 | 6:00 | 1.4 | SW |
| 19-Oct-2017 | 7:00 | 1.6 | WSW |
| 19-Oct-2017 | 8:00 | 1.6 | WNW |
| 19-Oct-2017 | 9:00 | 1.6 | SSE |
| 19-Oct-2017 | 10:00 | 2 | SSE |
| 19-Oct-2017 | 11:00 | 2.2 | S |
| 19-Oct-2017 | 12:00 | 2.3 | SSE |
| 19-Oct-2017 | 13:00 | 2.2 | SSE |
| 19-Oct-2017 | 14:00 | 2.3 | SE |
| 19-Oct-2017 | 15:00 | 2.2 | ESE |
| 19-Oct-2017 | 16:00 | 2 | ENE |
| 19-Oct-2017 | 17:00 | 2.3 | S |
| 19-Oct-2017 | 18:00 | 2.1 | ENE |
| 19-Oct-2017 | 19:00 | 1.7 | WNW |
| 19-Oct-2017 | 20:00 | 1.2 | WSW |
| 19-Oct-2017 | 21:00 | 1.2 | WNW |
| 19-Oct-2017 | 22:00 | 1.5 | ENE |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 19-Oct-2017 | 23:00 | 1.3 | ENE |
| 20-Oct-2017 | 0:00 | 1.2 | ENE |
| 20-Oct-2017 | 1:00 | 1.4 | ENE |
| 20-Oct-2017 | 2:00 | 1.4 | S |
| 20-Oct-2017 | 3:00 | 1.2 | SSE |
| 20-Oct-2017 | 4:00 | 1.3 | S |
| 20-Oct-2017 | 5:00 | 1.3 | S |
| 20-Oct-2017 | 6:00 | 1.3 | S |
| 20-Oct-2017 | 7:00 | 1.3 | SE |
| 20-Oct-2017 | 8:00 | 1.6 | N |
| 20-Oct-2017 | 9:00 | 1.7 | SSW |
| 20-Oct-2017 | 10:00 | 1.8 | NE |
| 20-Oct-2017 | 11:00 | 2 | NE |
| 20-Oct-2017 | 12:00 | 2.1 | E |
| 20-Oct-2017 | 13:00 | 2.2 | NNE |
| 20-Oct-2017 | 14:00 | 2.2 | ENE |
| 20-Oct-2017 | 15:00 | 2.1 | ENE |
| 20-Oct-2017 | 16:00 | 2.1 | ENE |
| 20-Oct-2017 | 17:00 | 2 | NNE |
| 20-Oct-2017 | 18:00 | 1.9 | E |
| 20-Oct-2017 | 19:00 | 1.7 | ESE |
| 20-Oct-2017 | 20:00 | 1.6 | ENE |
| 20-Oct-2017 | 21:00 | 1.6 | ENE |
| 20-Oct-2017 | 22:00 | 1.6 | NNE |
| 20-Oct-2017 | 23:00 | 1.7 | ENE |
| 21-Oct-2017 | 0:00 | 1.5 | NNE |
| 21-Oct-2017 | 1:00 | 1.5 | NNE |
| 21-Oct-2017 | 2:00 | 1.4 | NE |
| 21-Oct-2017 | 3:00 | 1.6 | NE |
| 21-Oct-2017 | 4:00 | 1.6 | NE |
| 21-Oct-2017 | 5:00 | 1.5 | NE |
| 21-Oct-2017 | 6:00 | 1.9 | NE |
| 21-Oct-2017 | 7:00 | 2 | ENE |
| 21-Oct-2017 | 8:00 | 1.8 | E |
| 21-Oct-2017 | 9:00 | 2.1 | NE |
| 21-Oct-2017 | 10:00 | 2.3 | N |
| 21-Oct-2017 | 11:00 | 2.4 | NNW |
| 21-Oct-2017 | 12:00 | 2.5 | N |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 21-Oct-2017 | 13:00 | 2.4 | NE |
| 21-Oct-2017 | 14:00 | 2.4 | NW |
| 21-Oct-2017 | 15:00 | 2.6 | NW |
| 21-Oct-2017 | 16:00 | 2.6 | NW |
| 21-Oct-2017 | 17:00 | 2.4 | NW |
| 21-Oct-2017 | 18:00 | 2.7 | W |
| 21-Oct-2017 | 19:00 | 2.1 | NE |
| 21-Oct-2017 | 20:00 | 2 | NE |
| 21-Oct-2017 | 21:00 | 1.9 | ENE |
| 21-Oct-2017 | 22:00 | 1.8 | NE |
| 21-Oct-2017 | 23:00 | 1.3 | WSW |
| 22-Oct-2017 | 0:00 | 1.5 | NE |
| 22-Oct-2017 | 1:00 | 1.5 | WSW |
| 22-Oct-2017 | 2:00 | 1.5 | WSW |
| 22-Oct-2017 | 3:00 | 1.1 | ENE |
| 22-Oct-2017 | 4:00 | 1.1 | WSW |
| 22-Oct-2017 | 5:00 | 1.2 | ENE |
| 22-Oct-2017 | 6:00 | 1.1 | N |
| 22-Oct-2017 | 7:00 | 1.3 | NNE |
| 22-Oct-2017 | 8:00 | 1.3 | NNW |
| 22-Oct-2017 | 9:00 | 1.4 | NE |
| 22-Oct-2017 | 10:00 | 1.5 | NE |
| 22-Oct-2017 | 11:00 | 1.6 | N |
| 22-Oct-2017 | 12:00 | 1.9 | NE |
| 22-Oct-2017 | 13:00 | 2.1 | NNE |
| 22-Oct-2017 | 14:00 | 2.1 | NNE |
| 22-Oct-2017 | 15:00 | 2 | NE |
| 22-Oct-2017 | 16:00 | 2.2 | NE |
| 22-Oct-2017 | 17:00 | 2.1 | NNE |
| 22-Oct-2017 | 18:00 | 1.7 | NE |
| 22-Oct-2017 | 19:00 | 1.6 | NE |
| 22-Oct-2017 | 20:00 | 1.4 | NE |
| 22-Oct-2017 | 21:00 | 1.5 | N |
| 22-Oct-2017 | 22:00 | 1.3 | N |
| 22-Oct-2017 | 23:00 | 1.6 | NE |
| 23-Oct-2017 | 0:00 | 1.7 | SW |
| 23-Oct-2017 | 1:00 | 1.7 | S |
| 23-Oct-2017 | 2:00 | 1.6 | S |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 23-Oct-2017 | 3:00 | 1.7 | SSE |
| 23-Oct-2017 | 4:00 | 1.8 | SW |
| 23-Oct-2017 | 5:00 | 1.9 | N |
| 23-Oct-2017 | 6:00 | 2.3 | SW |
| 23-Oct-2017 | 7:00 | 1.8 | SW |
| 23-Oct-2017 | 8:00 | 1.6 | SSW |
| 23-Oct-2017 | 9:00 | 1.7 | WSW |
| 23-Oct-2017 | 10:00 | 2 | SSE |
| 23-Oct-2017 | 11:00 | 2.1 | SW |
| 23-Oct-2017 | 12:00 | 2.1 | SSE |
| 23-Oct-2017 | 13:00 | 2 | SSE |
| 23-Oct-2017 | 14:00 | 2 | SSW |
| 23-Oct-2017 | 15:00 | 2 | WSW |
| 23-Oct-2017 | 16:00 | 1.9 | W |
| 23-Oct-2017 | 17:00 | 1.7 | WSW |
| 23-Oct-2017 | 18:00 | 1.8 | SE |
| 23-Oct-2017 | 19:00 | 1.6 | SW |
| 23-Oct-2017 | 20:00 | 1.6 | SW |
| 23-Oct-2017 | 21:00 | 1.5 | SW |
| 23-Oct-2017 | 22:00 | 1.5 | SW |
| 23-Oct-2017 | 23:00 | 1.5 | S |
| 24-Oct-2017 | 0:00 | 1.7 | SE |
| 24-Oct-2017 | 1:00 | 1.7 | S |
| 24-Oct-2017 | 2:00 | 1.7 | SW |
| 24-Oct-2017 | 3:00 | 1.6 | SW |
| 24-Oct-2017 | 4:00 | 1.5 | SSW |
| 24-Oct-2017 | 5:00 | 1.5 | SSW |
| 24-Oct-2017 | 6:00 | 1.4 | SSW |
| 24-Oct-2017 | 7:00 | 1.5 | WSW |
| 24-Oct-2017 | 8:00 | 1.4 | WSW |
| 24-Oct-2017 | 9:00 | 1.7 | SW |
| 24-Oct-2017 | 10:00 | 2 | WSW |
| 24-Oct-2017 | 11:00 | 2.3 | SW |
| 24-Oct-2017 | 12:00 | 2.2 | SW |
| 24-Oct-2017 | 13:00 | 2.2 | SW |
| 24-Oct-2017 | 14:00 | 2.2 | SW |
| 24-Oct-2017 | 15:00 | 2.2 | SW |
| 24-Oct-2017 | 16:00 | 2.2 | W |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 24-Oct-2017 | 17:00 | 2.3 | W |
| 24-Oct-2017 | 18:00 | 1.9 | SSW |
| 24-Oct-2017 | 19:00 | 2.1 | E |
| 24-Oct-2017 | 20:00 | 1.4 | WSW |
| 24-Oct-2017 | 21:00 | 1.4 | WSW |
| 24-Oct-2017 | 22:00 | 1.4 | SW |
| 24-Oct-2017 | 23:00 | 1.4 | WSW |
| 25-Oct-2017 | 0:00 | 1.6 | SW |
| 25-Oct-2017 | 1:00 | 1.7 | SW |
| 25-Oct-2017 | 2:00 | 1.6 | NNW |
| 25-Oct-2017 | 3:00 | 1.3 | NNW |
| 25-Oct-2017 | 4:00 | 1.3 | NW |
| 25-Oct-2017 | 5:00 | 1.5 | SE |
| 25-Oct-2017 | 6:00 | 1.5 | ESE |
| 25-Oct-2017 | 7:00 | 1.3 | SSE |
| 25-Oct-2017 | 8:00 | 1.5 | SSW |
| 25-Oct-2017 | 9:00 | 1.7 | SSE |
| 25-Oct-2017 | 10:00 | 1.4 | SSE |
| 25-Oct-2017 | 11:00 | 2.1 | E |
| 25-Oct-2017 | 12:00 | 1.9 | SE |
| 25-Oct-2017 | 13:00 | 2.1 | SE |
| 25-Oct-2017 | 14:00 | 1.7 | NE |
| 25-Oct-2017 | 15:00 | 1.8 | ESE |
| 25-Oct-2017 | 16:00 | 1.9 | ENE |
| 25-Oct-2017 | 17:00 | 2 | ESE |
| 25-Oct-2017 | 18:00 | 1.3 | S |
| 25-Oct-2017 | 19:00 | 1.5 | SSE |
| 25-Oct-2017 | 20:00 | 1.6 | SSE |
| 25-Oct-2017 | 21:00 | 1.5 | ESE |
| 25-Oct-2017 | 22:00 | 1.6 | ENE |
| 25-Oct-2017 | 23:00 | 1.6 | NNW |
| 26-Oct-2017 | 0:00 | 1.5 | NW |
| 26-Oct-2017 | 1:00 | 1.3 | WSW |
| 26-Oct-2017 | 2:00 | 1.4 | SSE |
| 26-Oct-2017 | 3:00 | 1.3 | SSE |
| 26-Oct-2017 | 4:00 | 1.3 | SE |
| 26-Oct-2017 | 5:00 | 1.2 | ESE |
| 26-Oct-2017 | 6:00 | 1 | SSE |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 26-Oct-2017 | 7:00 | 1.1 | SSE |
| 26-Oct-2017 | 8:00 | 1.1 | E |
| 26-Oct-2017 | 9:00 | 1.5 | ENE |
| 26-Oct-2017 | 10:00 | 1.5 | ENE |
| 26-Oct-2017 | 11:00 | 1.7 | ENE |
| 26-Oct-2017 | 12:00 | 2 | SE |
| 26-Oct-2017 | 13:00 | 2.3 | SE |
| 26-Oct-2017 | 14:00 | 2.2 | S |
| 26-Oct-2017 | 15:00 | 2 | SSE |
| 26-Oct-2017 | 16:00 | 1.9 | SE |
| 26-Oct-2017 | 17:00 | 1.7 | W |
| 26-Oct-2017 | 18:00 | 1.2 | ENE |
| 26-Oct-2017 | 19:00 | 1.2 | SW |
| 26-Oct-2017 | 20:00 | 1 | ENE |
| 26-Oct-2017 | 21:00 | 1.4 | ENE |
| 26-Oct-2017 | 22:00 | 1.2 | E |
| 26-Oct-2017 | 23:00 | 1.2 | WNW |
| 27-Oct-2017 | 0:00 | 1.3 | WSW |
| 27-Oct-2017 | 1:00 | 1 | SW |
| 27-Oct-2017 | 2:00 | 1 | ESE |
| 27-Oct-2017 | 3:00 | 1.1 | NE |
| 27-Oct-2017 | 4:00 | 1.2 | WNW |
| 27-Oct-2017 | 5:00 | 1.3 | WSW |
| 27-Oct-2017 | 6:00 | 1.2 | S |
| 27-Oct-2017 | 7:00 | 1.2 | ENE |
| 27-Oct-2017 | 8:00 | 1.3 | NNW |
| 27-Oct-2017 | 9:00 | 1.4 | SSE |
| 27-Oct-2017 | 10:00 | 1.4 | SE |
| 27-Oct-2017 | 11:00 | 1.6 | SSE |
| 27-Oct-2017 | 12:00 | 1.9 | NE |
| 27-Oct-2017 | 13:00 | 2 | ESE |
| 27-Oct-2017 | 14:00 | 1.8 | NE |
| 27-Oct-2017 | 15:00 | 2 | SSE |
| 27-Oct-2017 | 16:00 | 1.7 | SE |
| 27-Oct-2017 | 17:00 | 1.6 | ESE |
| 27-Oct-2017 | 18:00 | 1.6 | NE |
| 27-Oct-2017 | 19:00 | 1.6 | ENE |
| 27-Oct-2017 | 20:00 | 1.6 | WNW |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 27-Oct-2017 | 21:00 | 1.5 | ENE |
| 27-Oct-2017 | 22:00 | 1.4 | ENE |
| 27-Oct-2017 | 23:00 | 1.4 | N |
| 28-Oct-2017 | 0:00 | 1.4 | NE |
| 28-Oct-2017 | 1:00 | 1.2 | E |
| 28-Oct-2017 | 2:00 | 1.2 | WNW |
| 28-Oct-2017 | 3:00 | 1.5 | W |
| 28-Oct-2017 | 4:00 | 1.3 | NNE |
| 28-Oct-2017 | 5:00 | 1.3 | ENE |
| 28-Oct-2017 | 6:00 | 1.1 | E |
| 28-Oct-2017 | 7:00 | 1.4 | S |
| 28-Oct-2017 | 8:00 | 1.5 | SSW |
| 28-Oct-2017 | 9:00 | 1.5 | WNW |
| 28-Oct-2017 | 10:00 | 1.7 | NW |
| 28-Oct-2017 | 11:00 | 1.7 | WNW |
| 28-Oct-2017 | 12:00 | 2 | WNW |
| 28-Oct-2017 | 13:00 | 2 | NNE |
| 28-Oct-2017 | 14:00 | 1.9 | NW |
| 28-Oct-2017 | 15:00 | 2 | S |
| 28-Oct-2017 | 16:00 | 1.9 | SE |
| 28-Oct-2017 | 17:00 | 1.9 | SSE |
| 28-Oct-2017 | 18:00 | 1.6 | SW |
| 28-Oct-2017 | 19:00 | 1.3 | WNW |
| 28-Oct-2017 | 20:00 | 1.2 | NNE |
| 28-Oct-2017 | 21:00 | 1.2 | NW |
| 28-Oct-2017 | 22:00 | 1.1 | SSW |
| 28-Oct-2017 | 23:00 | 1.3 | WNW |
| 29-Oct-2017 | 0:00 | 1.4 | WNW |
| 29-Oct-2017 | 1:00 | 1.6 | NW |
| 29-Oct-2017 | 2:00 | 1.7 | NNW |
| 29-Oct-2017 | 3:00 | 1.5 | NW |
| 29-Oct-2017 | 4:00 | 1.6 | NNW |
| 29-Oct-2017 | 5:00 | 1.4 | S |
| 29-Oct-2017 | 6:00 | 1.5 | WNW |
| 29-Oct-2017 | 7:00 | 1.3 | S |
| 29-Oct-2017 | 8:00 | 1.3 | SW |
| 29-Oct-2017 | 9:00 | 1.3 | NW |
| 29-Oct-2017 | 10:00 | 1.7 | NNW |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 29-Oct-2017 | 11:00 | 1.9 | NW |
| 29-Oct-2017 | 12:00 | 1.9 | NW |
| 29-Oct-2017 | 13:00 | 2 | S |
| 29-Oct-2017 | 14:00 | 1.9 | WNW |
| 29-Oct-2017 | 15:00 | 1.9 | NW |
| 29-Oct-2017 | 16:00 | 1.9 | NW |
| 29-Oct-2017 | 17:00 | 1.7 | NW |
| 29-Oct-2017 | 18:00 | 1.4 | WNW |
| 29-Oct-2017 | 19:00 | 1.4 | SE |
| 29-Oct-2017 | 20:00 | 1.5 | NNW |
| 29-Oct-2017 | 21:00 | 1.4 | WNW |
| 29-Oct-2017 | 22:00 | 1.2 | ENE |
| 29-Oct-2017 | 23:00 | 1.2 | ENE |
| 30-Oct-2017 | 0:00 | 1.2 | WSW |
| 30-Oct-2017 | 1:00 | 1.1 | SSE |
| 30-Oct-2017 | 2:00 | 1 | SW |
| 30-Oct-2017 | 3:00 | 1.2 | ENE |
| 30-Oct-2017 | 4:00 | 1.1 | W |
| 30-Oct-2017 | 5:00 | 1 | SSE |
| 30-Oct-2017 | 6:00 | 0.9 | ENE |
| 30-Oct-2017 | 7:00 | 1 | SSE |
| 30-Oct-2017 | 8:00 | 1 | NNE |
| 30-Oct-2017 | 9:00 | 1 | ENE |
| 30-Oct-2017 | 10:00 | 1.1 | W |
| 30-Oct-2017 | 11:00 | 1.1 | WSW |
| 30-Oct-2017 | 12:00 | 1.4 | SW |
| 30-Oct-2017 | 13:00 | 1.6 | W |
| 30-Oct-2017 | 14:00 | 1.5 | N |
| 30-Oct-2017 | 15:00 | 1.6 | NE |
| 30-Oct-2017 | 16:00 | 1.4 | WSW |
| 30-Oct-2017 | 17:00 | 1.4 | SW |
| 30-Oct-2017 | 18:00 | 1.5 | SW |
| 30-Oct-2017 | 19:00 | 1.4 | E |
| 30-Oct-2017 | 20:00 | 1.3 | ESE |
| 30-Oct-2017 | 21:00 | 1.2 | WSW |
| 30-Oct-2017 | 22:00 | 1.1 | SSW |
| 30-Oct-2017 | 23:00 | 1.4 | W |
| 31-Oct-2017 | 0:00 | 1.6 | NE |

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

| | | | |
|-------------|-------|-----|-----|
| 31-Oct-2017 | 1:00 | 1.8 | E |
| 31-Oct-2017 | 2:00 | 1.8 | WSW |
| 31-Oct-2017 | 3:00 | 1.6 | SSW |
| 31-Oct-2017 | 4:00 | 1.9 | W |
| 31-Oct-2017 | 5:00 | 2.3 | WSW |
| 31-Oct-2017 | 6:00 | 1.9 | W |
| 31-Oct-2017 | 7:00 | 1.7 | SW |
| 31-Oct-2017 | 8:00 | 1.5 | ENE |
| 31-Oct-2017 | 9:00 | 1.8 | NE |
| 31-Oct-2017 | 10:00 | 1.8 | NE |
| 31-Oct-2017 | 11:00 | 1.7 | ENE |
| 31-Oct-2017 | 12:00 | 2.1 | NE |
| 31-Oct-2017 | 13:00 | 1.9 | NE |
| 31-Oct-2017 | 14:00 | 1.5 | W |
| 31-Oct-2017 | 15:00 | 1.1 | ENE |
| 31-Oct-2017 | 16:00 | 0.9 | WNW |
| 31-Oct-2017 | 17:00 | 0.7 | N |
| 31-Oct-2017 | 18:00 | 0.7 | SW |
| 31-Oct-2017 | 19:00 | 1.2 | WNW |
| 31-Oct-2017 | 20:00 | 1.2 | W |
| 31-Oct-2017 | 21:00 | 1.2 | WSW |
| 31-Oct-2017 | 22:00 | 0.6 | SSW |
| 31-Oct-2017 | 23:00 | 0.5 | SSW |

**APPENDIX D
ENVIRONMENTAL MONITORING
SCHEDULES**

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Impact Air Quality and Noise Monitoring Schedule (October 2017)

| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|---------------|---|--|--|---|--|---------------|
| 1-Oct | 2-Oct | 3-Oct | 4-Oct | 5-Oct | 6-Oct | 7-Oct |
| | | 1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM1, CM3, CM5, CM6(A), CM7(A), CM8(A)] | 24 hr TSP | | 1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM2, CM4] | |
| 8-Oct | 9-Oct | 10-Oct | 11-Oct | 12-Oct | 13-Oct | 14-Oct |
| | 1 hr TSP X3 [AM5(A), AM6(A)] | | | 1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM3, CM4, CM5] | 1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM1, CM6(A), CM7(A), CM8(A)] | |
| 15-Oct | 16-Oct | 17-Oct | 18-Oct | 19-Oct | 20-Oct | 21-Oct |
| | | | 1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4] | 1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)] | | |
| 22-Oct | 23-Oct | 24-Oct | 25-Oct | 26-Oct | 27-Oct | 28-Oct |
| | | 1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM3, CM4, CM5] | 1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)] | | | |
| 29-Oct | 30-Oct | 31-Oct | | | | |
| | 1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4] | 1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)] | | | | |

Air Quality Monitoring Station

AM1 - Tin Hau Temple
AM2 - Sai Tso Wan Recreation Ground
AM3 - Yau Lai Estate Bik Lai House
AM4⁽¹⁾ - Sitting-out Area at Cha Kwo Ling Village
AM4(A)⁽²⁾ - Cha Kwo Ling Public Cargo Working Area Administrative Office
AM5(A) - Tseung Kwan O DSD Desilting Compound
AM6(A) - Park Central, L1/F Open Space Area

Noise Monitoring Station

CM1 - Nga Lai House, Yau Lai Estate Phase 1, Yau Tong
CM2 - Bik Lai House, Yau Lai Estate Phase 1, Yau Tong
CM3 - Block S, Yau Lai Estate Phase 5, Yau Tong
CM4 - Tin Hau Temple, Cha Kwo Ling
CM5 - CCC Kei Faat Primary School, Yau Tong
CM6(A) - Site Boundary of Contract No. NE/2015/02 near Tower 1, Ocean Shores
CM7(A) - Site Boundary of Contract No. NE/2015/02 near Tower 7, Ocean Shores
CM8(A) - Park Central, L1/F Open Space Area

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Impact Groundwater Quality Monitoring Schedule (October 2017)

| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|--------|--------|---------|-----------|--------------------------------|--------|----------|
| 1-Oct | 2-Oct | 3-Oct | 4-Oct | 5-Oct | 6-Oct | 7-Oct |
| | | | | | | |
| 8-Oct | 9-Oct | 10-Oct | 11-Oct | 12-Oct | 13-Oct | 14-Oct |
| | | | | Groundwater Quality Monitoring | | |
| 15-Oct | 16-Oct | 17-Oct | 18-Oct | 19-Oct | 20-Oct | 21-Oct |
| | | | | | | |
| 22-Oct | 23-Oct | 24-Oct | 25-Oct | 26-Oct | 27-Oct | 28-Oct |
| | | | | Groundwater Quality Monitoring | | |
| 29-Oct | 30-Oct | 31-Oct | | | | |
| | | | | | | |

Monitoring Location:

Stream 1, Stream 2, Stream 3

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Impact Water Quality Monitoring Schedule (October 2017)

| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|---------------|---------------------------------|---------|----------------------------------|--------------|-----------------------------------|---------------------------------|
| 1-Oct | 2-Oct | 3-Oct | 4-Oct | 5-Oct | 6-Oct | 7-Oct |
| | Mid-Ebb 9:49 Mid-Flood 17:12 | | Mid-Ebb 11:13 Mid-Flood 17:53 | | Mid-Ebb 12:36 Mid-Flood 18:49 | |
| 8-Oct | 9-Oct | 10-Oct | 11-Oct | 12-Oct | 13-Oct | 14-Oct |
| | Mid-Flood 8:50 Mid-Ebb 14:42 | | Mid-Flood 10:58 Mid-Ebb 16:28 | | | Mid-Ebb 7:51 Mid-Flood 15:18 |
| 15-Oct | 16-Oct | 17-Oct | 18-Oct | 19-Oct | 20-Oct | 21-Oct |
| | Mid-Ebb 9:53 Mid-Flood 16:40 | | Mid-Ebb 11:25 Mid-Flood 17:39 | | Mid-Ebb 12:42 Mid-Flood 18:34 | |
| 22-Oct | 23-Oct | 24-Oct | 25-Oct | 26-Oct | 27-Oct | 28-Oct |
| | Mid-Flood 8:38 Mid-Ebb 14:25 | | Mid-Flood 10:18 Mid-Ebb 15:37 | | Mid-Ebb 4:21 # Mid-Flood 16:54 | |
| 29-Oct | 30-Oct | 31-Oct | | | | |
| | Mid-Ebb 8:06 Mid-Flood 15:48 | | | | | |

Monitoring Station:

C1, C2, G1, G2, G3, G4, M1, M2, M3, M4, M5, M6

Note #: It is proposed that there is no need for mid-ebb monitoring on 27 October 2017 based on the following reasons:

- a) There will be no marine works within the suitable tidal conditions (within ± 1.5 hour of the predicted mid-ebb or mid-flood tides).
- b) The above condition described in point a) occurs for 2 or more consecutive days.

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Tentative Impact Air Quality and Noise Monitoring Schedule (November 2017)

| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|--------|---|---|--|--|-------------------------------------|----------|
| | | | 1-Nov | 2-Nov | 3-Nov | 4-Nov |
| | | | 24 hr TSP | Noise [CM3, CM5] | 1 hr TSP X3 [AM1, AM2, AM3, AM4] | |
| 5-Nov | 6-Nov | 7-Nov | 8-Nov | 9-Nov | 10-Nov | 11-Nov |
| | 1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)] | Noise [CM3, CM5] 24 hr TSP | | 1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4] | 1 hr TSP X3 [AM5(A), AM6(A)] | |
| 12-Nov | 13-Nov | 14-Nov | 15-Nov | 16-Nov | 17-Nov | 18-Nov |
| | 24 hr TSP | Noise [CM3, CM5] | 1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4] | 1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)] | 24 hr TSP | |
| 19-Nov | 20-Nov | 21-Nov | 22-Nov | 23-Nov | 24-Nov | 25-Nov |
| | | 1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM3, CM4, CM5] | 1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)] | 24 hr TSP | | |
| 26-Nov | 27-Nov | 28-Nov | 29-Nov | 30-Nov | | |
| | 1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM3, CM4, CM5] | 1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)] | 24 hr TSP | | | |

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Air Quality Monitoring Station

AM1 - Tin Hau Temple
AM2 - Sai Tso Wan Recreation Ground
AM3 - Yau Lai Estate Bik Lai House
AM4⁽¹⁾ - Sitting-out Area at Cha Kwo Ling Village
AM4(A)⁽²⁾ - Cha Kwo Ling Public Cargo Working Area Administrative Office
AM5(A) - Tseung Kwan O DSD Desilting Compound
AM6(A) - Park Central, L1/F Open Space Area

Noise Monitoring Station

CM1 - Nga Lai House, Yau Lai Estate Phase 1, Yau Tong
CM2 - Bik Lai House, Yau Lai Estate Phase 1, Yau Tong
CM3 - Block S, Yau Lai Estate Phase 5, Yau Tong
CM4 - Tin Hau Temple, Cha Kwo Ling
CM5 - CCC Kei Faat Primary School, Yau Tong
CM6(A) - Site Boundary of Contract No. NE/2015/02 near Tower 1, Ocean Shores
CM7(A) - Site Boundary of Contract No. NE/2015/02 near Tower 7, Ocean Shores
CM8(A) - Park Central, L1/F Open Space Area

Note (1) For 1-hour TSP monitoring; (2) For 24-hour TSP monitoring

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Tentative Impact Groundwater Quality Monitoring Schedule (November 2017)

| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|---------------|--------|---------|-----------|-----------------------------------|--------|----------|
| | | | 1-Nov | 2-Nov | 3-Nov | 4-Nov |
| | | | | | | |
| 5-Nov | 6-Nov | 7-Nov | 8-Nov | 9-Nov | 10-Nov | 11-Nov |
| | | | | Groundwater Quality Monitoring | | |
| 12-Nov | 13-Nov | 14-Nov | 15-Nov | 16-Nov | 17-Nov | 18-Nov |
| | | | | | | |
| 19-Nov | 20-Nov | 21-Nov | 22-Nov | 23-Nov | 24-Nov | 25-Nov |
| | | | | Groundwater Quality Monitoring | | |
| 26-Nov | 27-Nov | 28-Nov | 29-Nov | 30-Nov | | |
| | | | | | | |

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Monitoring Location:

Stream 1, Stream 2, Stream 3

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Tentative Impact Water Quality Monitoring Schedule (November 2017)

| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|---------------|---------------------------------|---------------------------------|----------------------------------|---------------------------------|----------------------------------|----------|
| | | | 1-Nov | 2-Nov | 3-Nov | 4-Nov |
| | | | Mid-Ebb 9:51 Mid-Flood 16:38 | | Mid-Ebb 11:28 Mid-Flood 17:36 | |
| 5-Nov | 6-Nov | 7-Nov | 8-Nov | 9-Nov | 10-Nov | 11-Nov |
| | Mid-Flood 7:54 Mid-Ebb 13:39 | | Mid-Flood 9:50 Mid-Ebb 15:19 | | Mid-Flood 12:14 Mid-Ebb 17:22 | |
| 12-Nov | 13-Nov | 14-Nov | 15-Nov | 16-Nov | 17-Nov | 18-Nov |
| | Mid-Ebb 8:29 Mid-Flood 15:22 | | Mid-Ebb 10:16 Mid-Flood 16:32 | | Mid-Ebb 11:42 Mid-Flood 17:28 | |
| 19-Nov | 20-Nov | 21-Nov | 22-Nov | 23-Nov | 24-Nov | 25-Nov |
| | Mid-Flood 7:52 Mid-Ebb 13:38 | | Mid-Flood 9:15 Mid-Ebb 14:33 | | Mid-Flood 11:03 Mid-Ebb 15:53 | |
| 26-Nov | 27-Nov | 28-Nov | 29-Nov | 30-Nov | | |
| | | Mid-Ebb 6:49 Mid-Flood 14:44 | | Mid-Ebb 9:13 Mid-Flood 15:47 | | |

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Monitoring Station:

C1, C2, G1, G2, G3, G4, M1, M2, M3, M4, M5, M6

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Tentative Impact Water Quality Monitoring Schedule in Temporary Marine Embayment (November 2017)

| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|---------------|---------------------------------|---------------------------------|-----------|----------------------------------|--------|----------|
| | | | 1-Nov | 2-Nov | 3-Nov | 4-Nov |
| | | | | | | |
| 5-Nov | 6-Nov | 7-Nov | 8-Nov | 9-Nov | 10-Nov | 11-Nov |
| | Mid-Flood 7:53 Mid-Ebb 13:42 | | | | | |
| 12-Nov | 13-Nov | 14-Nov | 15-Nov | 16-Nov | 17-Nov | 18-Nov |
| | | | | Mid-Ebb 11:04 Mid-Flood 17:01 | | |
| 19-Nov | 20-Nov | 21-Nov | 22-Nov | 23-Nov | 24-Nov | 25-Nov |
| | | Mid-Flood 8:36 Mid-Ebb 14:14 | | | | |
| 26-Nov | 27-Nov | 28-Nov | 29-Nov | 30-Nov | | |
| | | Mid-Ebb 6:47 Mid-Flood 14:45 | | | | |

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Monitoring Station:

W1

**APPENDIX E
1-HOUR TSP MONITORING RESULTS
AND GRAPHICAL PRESENTATIONS**

Appendix E - 1-hour TSP Monitoring Results

| Location AM1 - Tin Hau Temple | | | |
|-------------------------------|-------|---------|--|
| Date | Time | Weather | Particulate Concentration ($\mu\text{g}/\text{m}^3$) |
| 6-Oct-17 | 9:00 | Sunny | 15.7 |
| 6-Oct-17 | 10:00 | Sunny | 17.9 |
| 6-Oct-17 | 11:00 | Sunny | 19.0 |
| 12-Oct-17 | 8:30 | Sunny | 131.2 |
| 12-Oct-17 | 9:30 | Sunny | 143.6 |
| 12-Oct-17 | 10:30 | Sunny | 149.6 |
| 18-Oct-17 | 8:30 | Sunny | 20.1 |
| 18-Oct-17 | 9:30 | Sunny | 20.1 |
| 18-Oct-17 | 10:30 | Sunny | 22.4 |
| 24-Oct-17 | 9:00 | Sunny | 127.4 |
| 24-Oct-17 | 10:00 | Sunny | 143.3 |
| 24-Oct-17 | 11:00 | Sunny | 136.4 |
| 30-Oct-17 | 8:55 | Sunny | 20.4 |
| 30-Oct-17 | 9:55 | Sunny | 12.9 |
| 30-Oct-17 | 10:55 | Sunny | 18.3 |
| Average | | | 66.6 |
| Maximum | | | 149.6 |
| Minimum | | | 12.9 |

| Location AM2 - Sai Tso Wan Recreation Ground | | | |
|--|-------|---------|--|
| Date | Time | Weather | Particulate Concentration ($\mu\text{g}/\text{m}^3$) |
| 6-Oct-17 | 13:00 | Sunny | 17.8 |
| 6-Oct-17 | 14:00 | Sunny | 11.1 |
| 6-Oct-17 | 15:00 | Sunny | 15.6 |
| 12-Oct-17 | 13:00 | Sunny | 143.5 |
| 12-Oct-17 | 14:00 | Sunny | 144.6 |
| 12-Oct-17 | 15:00 | Sunny | 154.1 |
| 18-Oct-17 | 8:45 | Sunny | 17.8 |
| 18-Oct-17 | 9:45 | Sunny | 18.9 |
| 18-Oct-17 | 10:45 | Sunny | 18.9 |
| 24-Oct-17 | 13:00 | Sunny | 199.3 |
| 24-Oct-17 | 14:00 | Sunny | 192.5 |
| 24-Oct-17 | 15:00 | Sunny | 190.5 |
| 30-Oct-17 | 8:35 | Sunny | 21.2 |
| 30-Oct-17 | 9:35 | Sunny | 21.2 |
| 30-Oct-17 | 10:35 | Sunny | 19.0 |
| Average | | | 79.1 |
| Maximum | | | 199.3 |
| Minimum | | | 11.1 |

Appendix E - 1-hour TSP Monitoring Results

| Location AM3 - Yau Lai Estate Bik Lai House | | | |
|---|-------|---------|--|
| Date | Time | Weather | Particulate Concentration ($\mu\text{g}/\text{m}^3$) |
| 6-Oct-17 | 13:00 | Sunny | 19.0 |
| 6-Oct-17 | 14:00 | Sunny | 21.3 |
| 6-Oct-17 | 15:00 | Sunny | 20.1 |
| 12-Oct-17 | 12:00 | Sunny | 122.1 |
| 12-Oct-17 | 13:00 | Sunny | 144.7 |
| 12-Oct-17 | 14:00 | Sunny | 138.4 |
| 18-Oct-17 | 13:00 | Sunny | 15.7 |
| 18-Oct-17 | 14:00 | Sunny | 19.0 |
| 18-Oct-17 | 15:00 | Sunny | 12.3 |
| 24-Oct-17 | 13:00 | Cloudy | 213.7 |
| 24-Oct-17 | 14:00 | Cloudy | 175.9 |
| 24-Oct-17 | 15:00 | Cloudy | 196.8 |
| 30-Oct-17 | 13:00 | Sunny | 21.2 |
| 30-Oct-17 | 14:00 | Sunny | 20.1 |
| 30-Oct-17 | 15:00 | Sunny | 21.2 |
| Average | | | 77.4 |
| Maximum | | | 213.7 |
| Minimum | | | 12.3 |




| Location AM4 - Sitting-out Area at Cha Kwo Ling Village | | | |
|---|-------|---------|--|
| Date | Time | Weather | Particulate Concentration ($\mu\text{g}/\text{m}^3$) |
| 6-Oct-17 | 9:00 | Sunny | 14.5 |
| 6-Oct-17 | 10:00 | Sunny | 15.6 |
| 6-Oct-17 | 11:00 | Sunny | 12.3 |
| 12-Oct-17 | 9:00 | Sunny | 176.6 |
| 12-Oct-17 | 10:00 | Sunny | 194.0 |
| 12-Oct-17 | 11:00 | Sunny | 177.7 |
| 18-Oct-17 | 13:25 | Sunny | 18.9 |
| 18-Oct-17 | 14:25 | Sunny | 21.2 |
| 18-Oct-17 | 15:25 | Sunny | 11.1 |
| 24-Oct-17 | 9:00 | Sunny | 126.4 |
| 24-Oct-17 | 10:00 | Sunny | 161.3 |
| 24-Oct-17 | 11:00 | Sunny | 167.6 |
| 30-Oct-17 | 13:00 | Sunny | 18.3 |
| 30-Oct-17 | 14:00 | Sunny | 19.4 |
| 30-Oct-17 | 15:00 | Sunny | 19.4 |
| Average | | | 77.0 |
| Maximum | | | 194.0 |
| Minimum | | | 11.1 |

Appendix E - 1-hour TSP Monitoring Results

| Location AM5(A) - Tseung Kwan O DSD Desilting Compound | | | |
|--|-------|---------|--|
| Date | Time | Weather | Particulate Concentration ($\mu\text{g}/\text{m}^3$) |
| 3-Oct-17 | 13:00 | Sunny | 85.2 |
| 3-Oct-17 | 14:00 | Sunny | 92.6 |
| 3-Oct-17 | 15:00 | Sunny | 84.3 |
| 9-Oct-17 | 13:00 | Sunny | 163.1 |
| 9-Oct-17 | 14:00 | Sunny | 165.1 |
| 9-Oct-17 | 15:00 | Sunny | 162.4 |
| 13-Oct-17 | 13:00 | Sunny | 129.2 |
| 13-Oct-17 | 14:00 | Sunny | 131.5 |
| 13-Oct-17 | 15:00 | Sunny | 134.2 |
| 19-Oct-17 | 13:00 | Fine | 209.8 |
| 19-Oct-17 | 14:00 | Fine | 200.5 |
| 19-Oct-17 | 15:00 | Fine | 185.6 |
| 25-Oct-17 | 9:00 | Sunny | 87.7 |
| 25-Oct-17 | 10:00 | Sunny | 94.1 |
| 25-Oct-17 | 11:00 | Sunny | 102.7 |
| 31-Oct-17 | 9:00 | Sunny | 250.7 |
| 31-Oct-17 | 10:00 | Sunny | 238.9 |
| 31-Oct-17 | 11:00 | Sunny | 233.0 |
| Average | | | 152.8 |
| Maximum | | | 250.7 |
| Minimum | | | 84.3 |




| Location AM6(A) - Park Central, L1/F Open Space Area | | | |
|--|-------|---------|--|
| Date | Time | Weather | Particulate Concentration ($\mu\text{g}/\text{m}^3$) |
| 3-Oct-17 | 13:00 | Sunny | 93.8 |
| 3-Oct-17 | 14:00 | Sunny | 86.4 |
| 3-Oct-17 | 15:00 | Sunny | 77.5 |
| 9-Oct-17 | 9:00 | Sunny | 130.5 |
| 9-Oct-17 | 10:00 | Sunny | 132.7 |
| 9-Oct-17 | 11:00 | Sunny | 135.9 |
| 13-Oct-17 | 9:00 | Sunny | 120.6 |
| 13-Oct-17 | 10:00 | Sunny | 118.0 |
| 13-Oct-17 | 11:00 | Sunny | 124.5 |
| 19-Oct-17 | 13:00 | Cloudy | 213.1 |
| 19-Oct-17 | 14:00 | Cloudy | 193.2 |
| 19-Oct-17 | 15:00 | Cloudy | 188.7 |
| 25-Oct-17 | 13:00 | Sunny | 93.7 |
| 25-Oct-17 | 14:00 | Sunny | 101.0 |
| 25-Oct-17 | 15:00 | Sunny | 106.4 |
| 31-Oct-17 | 13:23 | Sunny | 250.7 |
| 31-Oct-17 | 14:23 | Sunny | 216.2 |
| 31-Oct-17 | 15:23 | Sunny | 205.9 |
| Average | | | 143.8 |
| Maximum | | | 250.7 |
| Minimum | | | 77.5 |

1-hr TSP Concentration Levels

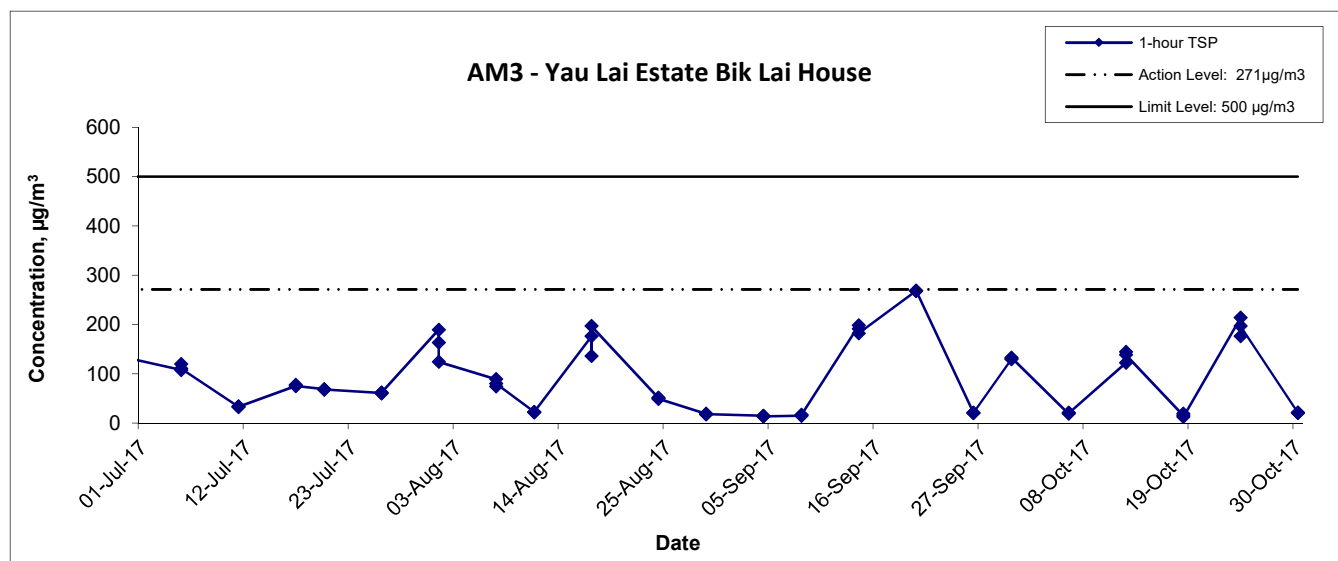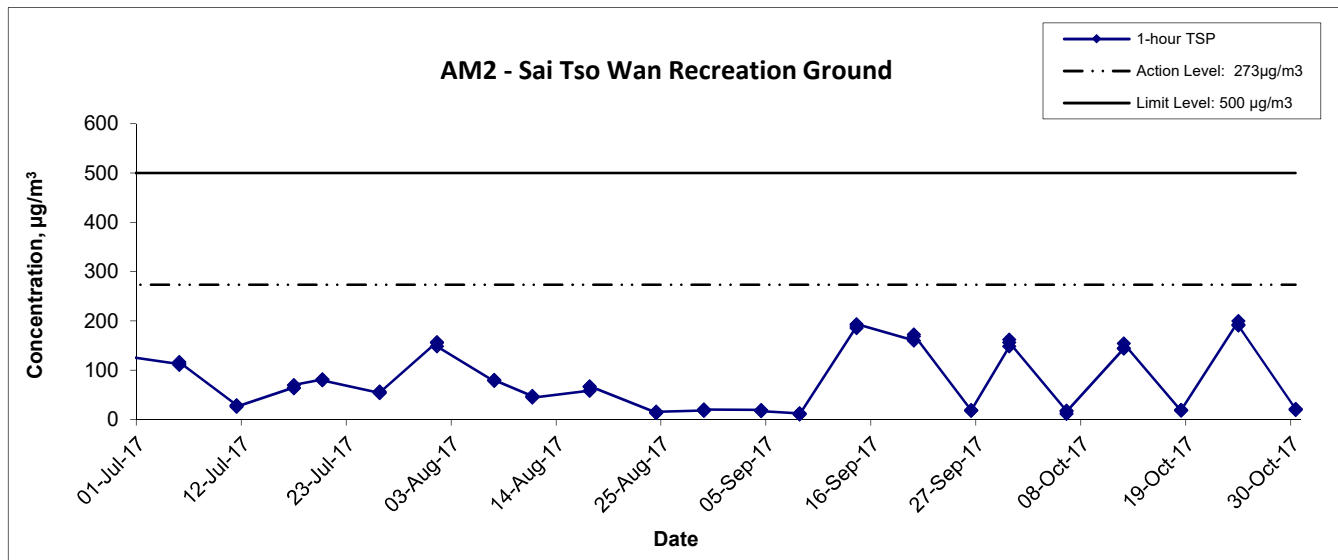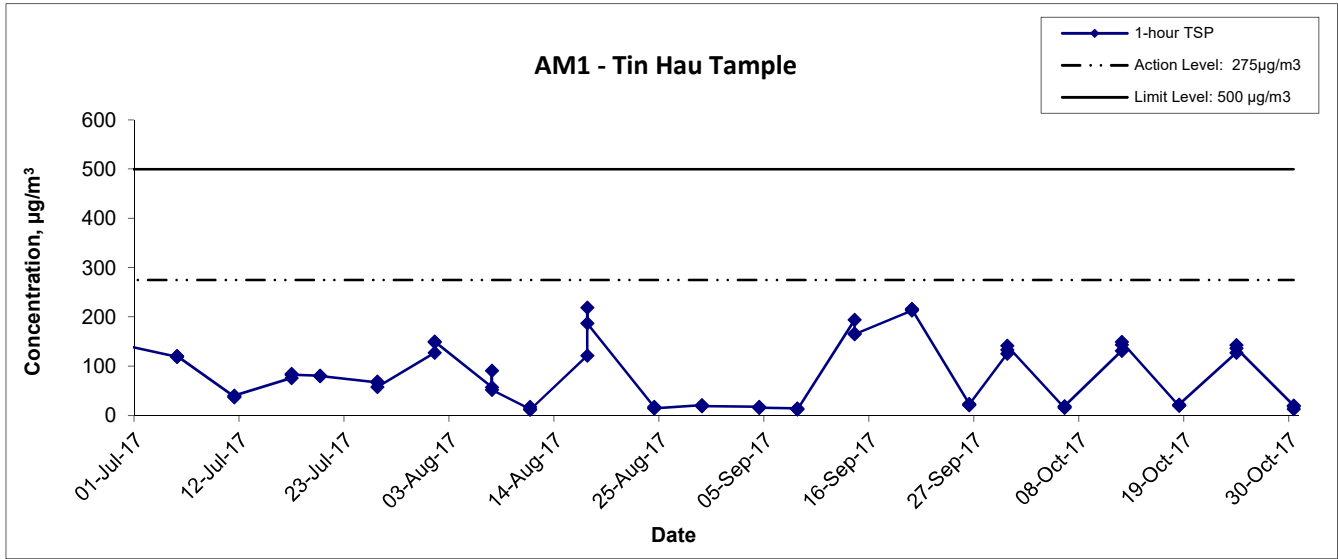

| | | | |
|---|----------------|------------------------|-----------------|
| Title Agreement No. CE/59/2015 (EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction Graphical Presentation of 1-hour TSP Monitoring Results | Scale N.T.S | Project No. MA16034 | CINOTECH |
| | Date Oct 17 | Appendix E | |

1-hr TSP Concentration Levels

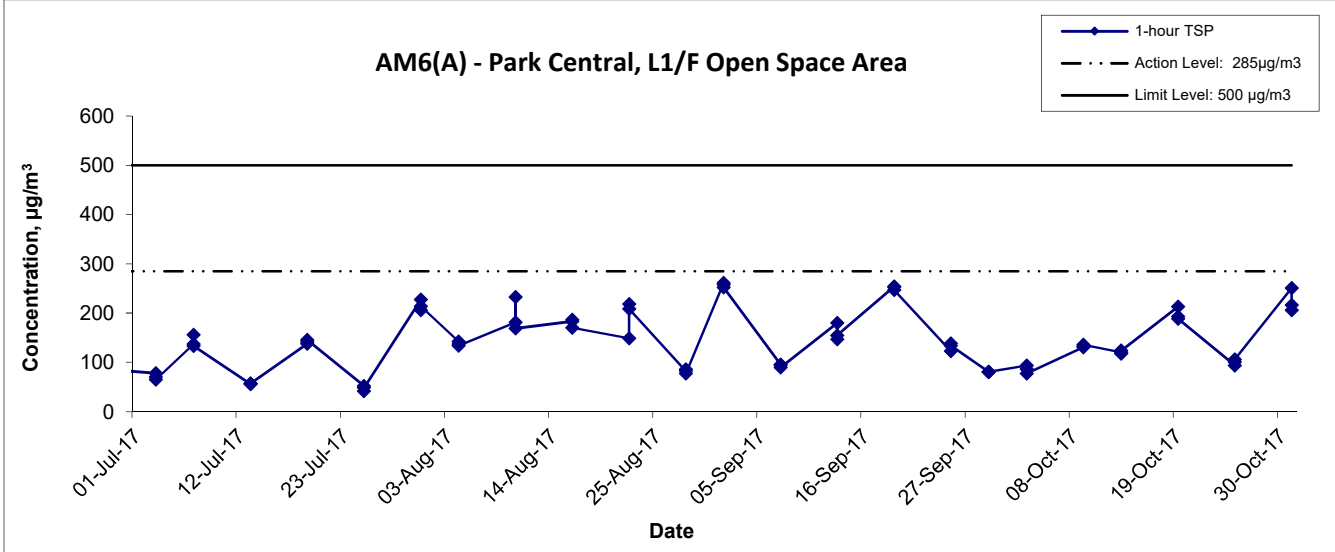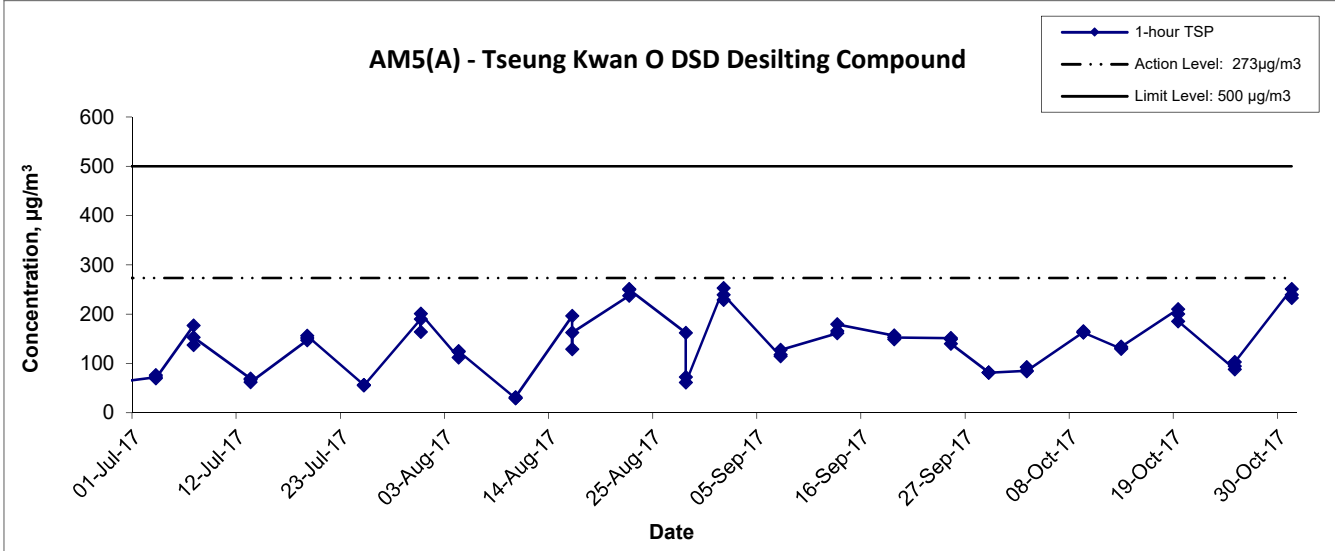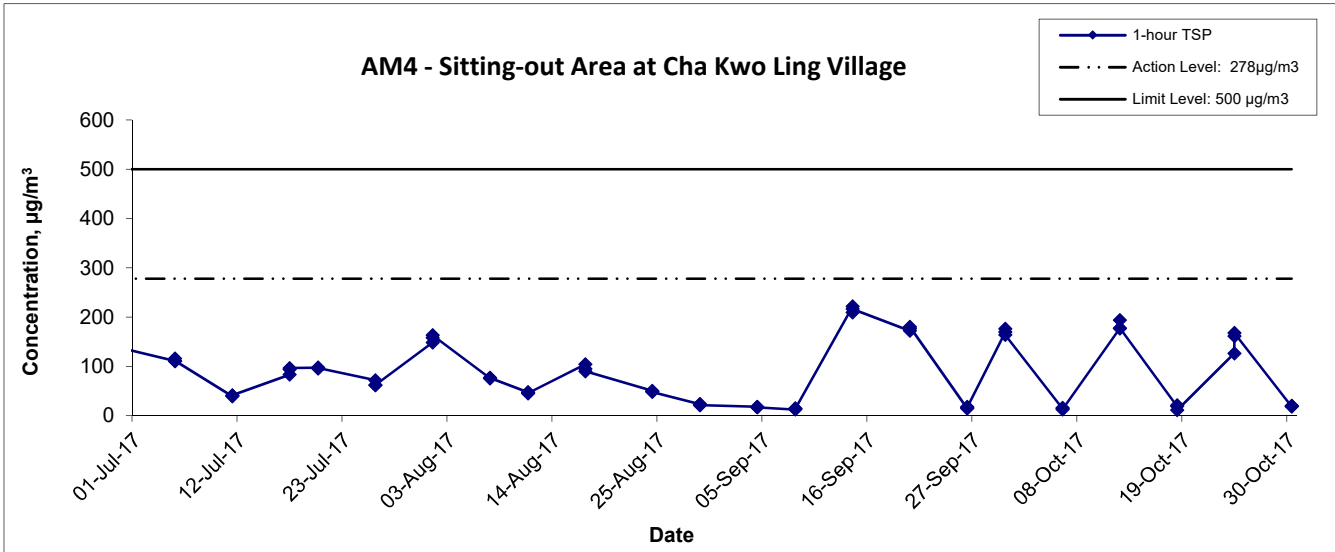

| | | | | |
|---|---|--------|-------------|----------|
| Title | Agreement No. CE/59/2015 (EP) | Scale | Project | CINOTECH |
| | Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction | N.T.S | No. MA16034 | |
| Graphical Presentation of 1-hour TSP Monitoring Results | | Date | Appendix | |
| | | Oct 17 | E | |

**APPENDIX F
24-HOUR TSP MONITORING RESULTS
AND GRAPHICAL PRESENTATIONS**

Appendix F - 24-hour TSP Monitoring Results

Location AM1 - Tin Hau Temple

| Start Date | Weather Condition | Air Temp. (K) | Atmospheric Pressure, Pa (mmHg) | Filter Weight (g) | | Particulate Weight (g) | Elapse Time | | Sampling Time(hrs.) | Flow Rate (m ³ /min.) | | Av. flow (m ³ /min) | Total vol. (m ³) | Conc. (µg/m ³) |
|------------|-------------------|---------------|---------------------------------|-------------------|--------|------------------------|-------------|--------|---------------------|----------------------------------|-------|--------------------------------|------------------------------|----------------------------|
| | | | | Initial | Final | | Initial | Final | | Initial | Final | | | |
| 4-Oct-17 | Cloudy | 302.5 | 762.7 | 3.3218 | 3.4218 | 0.1000 | 2531.0 | 2555.0 | 24.0 | 1.21 | 1.21 | 1.21 | 1749.1 | 57.2 |
| 10-Oct-17 | Sunny | 303.4 | 761.4 | 2.8751 | 2.9878 | 0.1127 | 2555.0 | 2579.0 | 24.0 | 1.21 | 1.21 | 1.21 | 1744.6 | 64.6 |
| 16-Oct-17 | Sunny | 301.7 | 758.7 | 2.8823 | 2.9533 | 0.0710 | 2579.0 | 2603.0 | 24.0 | 1.21 | 1.21 | 1.21 | 1746.6 | 40.7 |
| 20-Oct-17 | Sunny | 295.2 | 763.6 | 2.8483 | 2.9402 | 0.0919 | 2603.0 | 2627.0 | 24.0 | 1.23 | 1.23 | 1.23 | 1774.2 | 51.8 |
| 26-Oct-17 | Sunny | 297.6 | 766.3 | 2.9047 | 3.0706 | 0.1659 | 2627.0 | 2651.0 | 24.0 | 1.23 | 1.23 | 1.23 | 1769.7 | 93.7 |
| | | | | | | | | | | | | | Min | 40.7 |
| | | | | | | | | | | | | | Max | 93.7 |
| | | | | | | | | | | | | | Average | 61.6 |

Location AM2 - Sai Tso Wan Recreation Ground

| Start Date | Weather Condition | Air Temp. (K) | Atmospheric Pressure, Pa (mmHg) | Filter Weight (g) | | Particulate Weight (g) | Elapse Time | | Sampling Time(hrs.) | Flow Rate (m ³ /min.) | | Av. flow (m ³ /min) | Total vol. (m ³) | Conc. (µg/m ³) |
|------------|-------------------|---------------|---------------------------------|-------------------|--------|------------------------|-------------|---------|---------------------|----------------------------------|-------|--------------------------------|------------------------------|----------------------------|
| | | | | Initial | Final | | Initial | Final | | Initial | Final | | | |
| 4-Oct-17 | Cloudy | 303.1 | 762.7 | 3.3014 | 3.3494 | 0.0480 | 23495.3 | 23519.3 | 24.0 | 1.21 | 1.21 | 1.21 | 1746.3 | 27.5 |
| 10-Oct-17 | Sunny | 302.8 | 762.3 | 2.8833 | 2.9543 | 0.0710 | 23519.3 | 23543.3 | 24.0 | 1.21 | 1.21 | 1.21 | 1746.7 | 40.6 |
| 16-Oct-17 | Sunny | 302.4 | 758.4 | 2.8953 | 2.9471 | 0.0518 | 23543.3 | 23567.3 | 24.0 | 1.21 | 1.21 | 1.21 | 1743.3 | 29.7 |
| 20-Oct-17 | Sunny | 296.1 | 762.5 | 2.8752 | 2.9548 | 0.0796 | 23567.3 | 23591.3 | 24.0 | 1.23 | 1.23 | 1.23 | 1766.6 | 45.1 |
| 26-Oct-17 | Sunny | 297.9 | 766.1 | 2.8837 | 3.1734 | 0.2897 | 23591.3 | 23615.3 | 24.0 | 1.23 | 1.23 | 1.23 | 1765.4 | 164.1 |
| | | | | | | | | | | | | | Min | 27.5 |
| | | | | | | | | | | | | | Max | 164.1 |
| | | | | | | | | | | | | | Average | 61.4 |

Location AM3 - Yau Lai Estate, Bik Lai House

| Start Date | Weather Condition | Air Temp. (K) | Atmospheric Pressure, Pa (mmHg) | Filter Weight (g) | | Particulate Weight (g) | Elapse Time | | Sampling Time(hrs.) | Flow Rate (m ³ /min.) | | Av. flow (m ³ /min) | Total vol. (m ³) | Conc. (µg/m ³) |
|------------|-------------------|---------------|---------------------------------|-------------------|--------|------------------------|-------------|---------|---------------------|----------------------------------|-------|--------------------------------|------------------------------|----------------------------|
| | | | | Initial | Final | | Initial | Final | | Initial | Final | | | |
| 4-Oct-17 | Cloudy | 302.7 | 762.6 | 3.3215 | 3.3903 | 0.0688 | 12062.7 | 12086.7 | 24.0 | 1.21 | 1.21 | 1.21 | 1744.5 | 39.4 |
| 10-Oct-17 | Sunny | 303.4 | 761.7 | 2.8912 | 2.9805 | 0.0893 | 12086.7 | 12110.7 | 24.0 | 1.21 | 1.21 | 1.21 | 1741.2 | 51.3 |
| 16-Oct-17 | Sunny | 302.8 | 758.3 | 2.8558 | 2.8909 | 0.0351 | 12110.7 | 12134.7 | 24.0 | 1.21 | 1.21 | 1.21 | 1738.9 | 20.2 |
| 20-Oct-17 | Sunny | 295.5 | 762.9 | 2.8427 | 2.8750 | 0.0323 | 12134.7 | 12158.7 | 24.0 | 1.23 | 1.23 | 1.23 | 1767.3 | 18.3 |
| 26-Oct-17 | Sunny | 297.2 | 765.2 | 2.8727 | 2.9489 | 0.0762 | 12158.7 | 12182.7 | 24.0 | 1.23 | 1.23 | 1.23 | 1764.7 | 43.2 |
| | | | | | | | | | | | | | Min | 18.3 |
| | | | | | | | | | | | | | Max | 51.3 |
| | | | | | | | | | | | | | Average | 34.5 |

Appendix F - 24-hour TSP Monitoring Results

Location AM4(A) - Cha Kwo Ling Public Cargo Working Area Administrative Office

| Start Date | Weather Condition | Air Temp. (K) | Atmospheric Pressure, Pa (mmHg) | Filter Weight (g) | | Particulate Weight (g) | Elapse Time | | Sampling Time(hrs.) | Flow Rate (m ³ /min.) | | Av. flow (m ³ /min) | Total vol. (m ³) | Conc. (µg/m ³) |
|------------|-------------------|---------------|---------------------------------|-------------------|--------|------------------------|-------------|--------|---------------------|----------------------------------|-------|--------------------------------|------------------------------|----------------------------|
| | | | | Initial | Final | | Initial | Final | | Initial | Final | | | |
| 4-Oct-17 | Cloudy | 302.8 | 762.4 | 3.3270 | 3.5457 | 0.2187 | 9049.2 | 9073.2 | 24.0 | 1.21 | 1.21 | 1.21 | 1743.4 | 125.4 |
| 10-Oct-17 | Sunny | 302.0 | 761.7 | 2.8426 | 3.1131 | 0.2705 | 9073.2 | 9097.2 | 24.0 | 1.21 | 1.21 | 1.21 | 1745.3 | 155.0 |
| 16-Oct-17 | Sunny | 302.5 | 757.9 | 2.8837 | 3.0028 | 0.1191 | 9097.2 | 9121.2 | 24.0 | 1.21 | 1.21 | 1.21 | 1738.6 | 68.5 |
| 20-Oct-17 | Sunny | 296.2 | 762.6 | 2.8696 | 3.0407 | 0.1711 | 9121.2 | 9145.2 | 24.0 | 1.23 | 1.23 | 1.23 | 1765.5 | 96.9 |
| 26-Oct-17 | Sunny | 297.6 | 766.0 | 2.8770 | 3.2098 | 0.3328 | 9145.2 | 9169.2 | 24.0 | 1.23 | 1.23 | 1.23 | 1765.3 | 188.5 |
| | | | | | | | | | | | | | Min | 68.5 |
| | | | | | | | | | | | | | Max | 188.5 |
| | | | | | | | | | | | | | Average | 126.9 |




Location AM5(A) - Tseung Kwan O DSD Desilting Compound

| Start Date | Weather Condition | Air Temp. (K) | Atmospheric Pressure, Pa (mmHg) | Filter Weight (g) | | Particulate Weight (g) | Elapse Time | | Sampling Time(hrs.) | Flow Rate (m ³ /min.) | | Av. flow (m ³ /min) | Total vol. (m ³) | Conc. (µg/m ³) |
|------------|-------------------|---------------|---------------------------------|-------------------|--------|------------------------|-------------|---------|---------------------|----------------------------------|-------|--------------------------------|------------------------------|----------------------------|
| | | | | Initial | Final | | Initial | Final | | Initial | Final | | | |
| 4-Oct-17 | Sunny | 303.6 | 761.3 | 2.8889 | 2.9879 | 0.0990 | 22791.5 | 22815.5 | 24.0 | 1.23 | 1.22 | 1.23 | 1764.0 | 56.1 |
| 10-Oct-17 | Sunny | 302.5 | 760.9 | 2.8065 | 2.9962 | 0.1897 | 22815.5 | 22839.5 | 24.0 | 1.23 | 1.23 | 1.23 | 1766.8 | 107.4 |
| 16-Oct-17 | Cloudy | 301.7 | 757.6 | 2.8535 | 2.9339 | 0.0804 | 22839.5 | 22863.5 | 24.0 | 1.23 | 1.23 | 1.23 | 1765.3 | 45.5 |
| 20-Oct-17 | Sunny | 295.9 | 763.2 | 2.8699 | 2.9455 | 0.0756 | 22863.5 | 22887.5 | 24.0 | 1.24 | 1.24 | 1.24 | 1789.2 | 42.3 |
| 26-Oct-17 | Sunny | 297.5 | 765.5 | 2.8798 | 3.0816 | 0.2018 | 22887.5 | 22911.5 | 24.0 | 1.24 | 1.24 | 1.24 | 1787.1 | 112.9 |
| | | | | | | | | | | | | | Min | 42.3 |
| | | | | | | | | | | | | | Max | 112.9 |
| | | | | | | | | | | | | | Average | 72.8 |

Location AM6(A) - Park Central, L1/F Open Space Area




| Start Date | Weather Condition | Air Temp. (K) | Atmospheric Pressure, Pa (mmHg) | Filter Weight (g) | | Particulate Weight (g) | Elapse Time | | Sampling Time(hrs.) | Flow Rate (m ³ /min.) | | Av. flow (m ³ /min) | Total vol. (m ³) | Conc. (µg/m ³) |
|------------|-------------------|---------------|---------------------------------|-------------------|--------|------------------------|-------------|---------|---------------------|----------------------------------|-------|--------------------------------|------------------------------|----------------------------|
| | | | | Initial | Final | | Initial | Final | | Initial | Final | | | |
| 4-Oct-17 | Sunny | 302.5 | 761.7 | 2.8557 | 2.9402 | 0.0845 | 15851.8 | 15875.8 | 24.0 | 1.21 | 1.21 | 1.21 | 1743.2 | 48.5 |
| 10-Oct-17 | Sunny | 302.8 | 760.4 | 2.8130 | 2.8990 | 0.0860 | 15875.8 | 15899.8 | 24.0 | 1.21 | 1.21 | 1.21 | 1740.8 | 49.4 |
| 16-Oct-17 | Cloudy | 301.8 | 758.3 | 2.8796 | 2.9385 | 0.0589 | 15899.8 | 15923.8 | 24.0 | 1.21 | 1.21 | 1.21 | 1741.3 | 33.8 |
| 20-Oct-17 | Sunny | 295.0 | 763.1 | 2.8741 | 2.9429 | 0.0688 | 15923.8 | 15947.8 | 24.0 | 1.23 | 1.23 | 1.23 | 1766.9 | 38.9 |
| 26-Oct-17 | Sunny | 297.9 | 766.5 | 2.8934 | 3.0129 | 0.1195 | 15947.8 | 15971.8 | 24.0 | 1.22 | 1.22 | 1.22 | 1762.2 | 67.8 |
| | | | | | | | | | | | | | Min | 33.8 |
| | | | | | | | | | | | | | Max | 67.8 |
| | | | | | | | | | | | | | Average | 47.7 |

24-hr TSP Concentration Levels

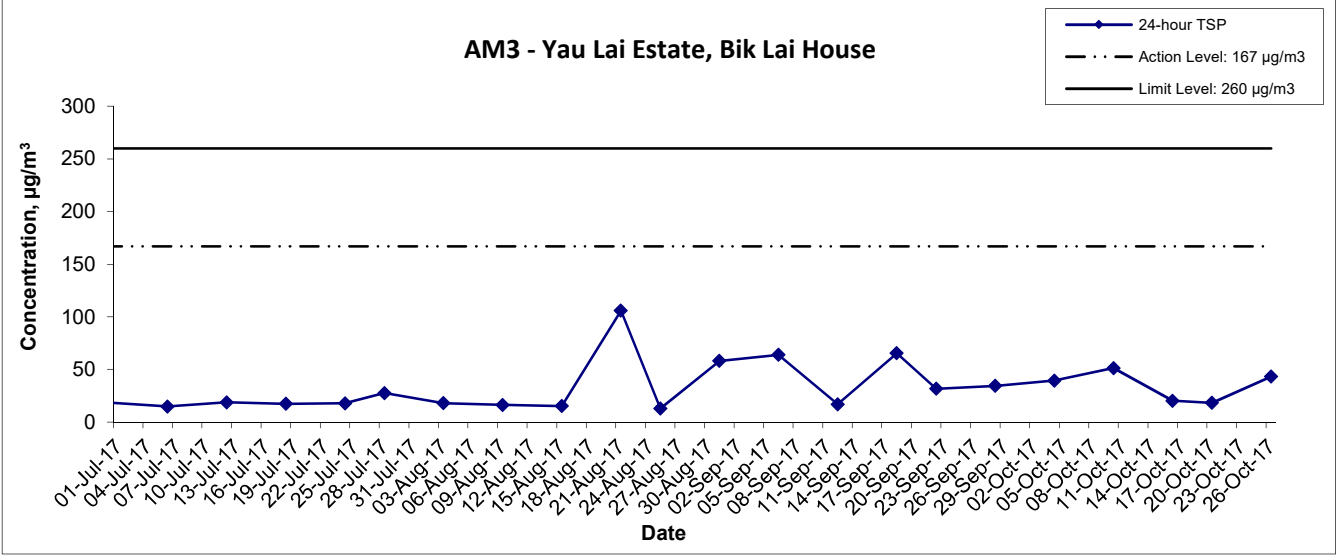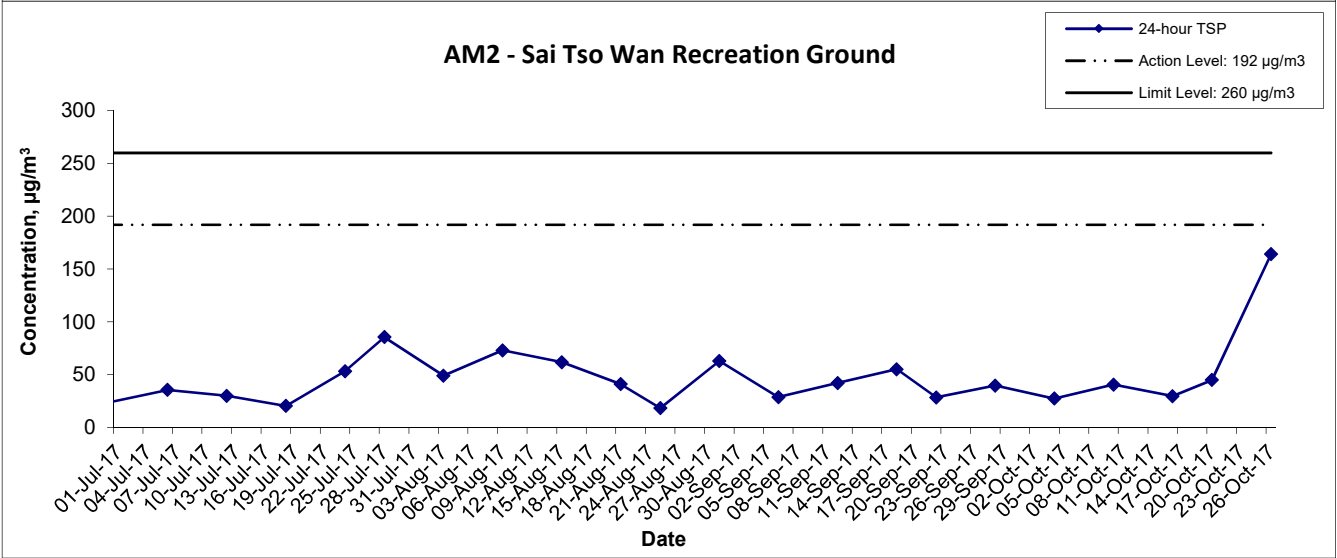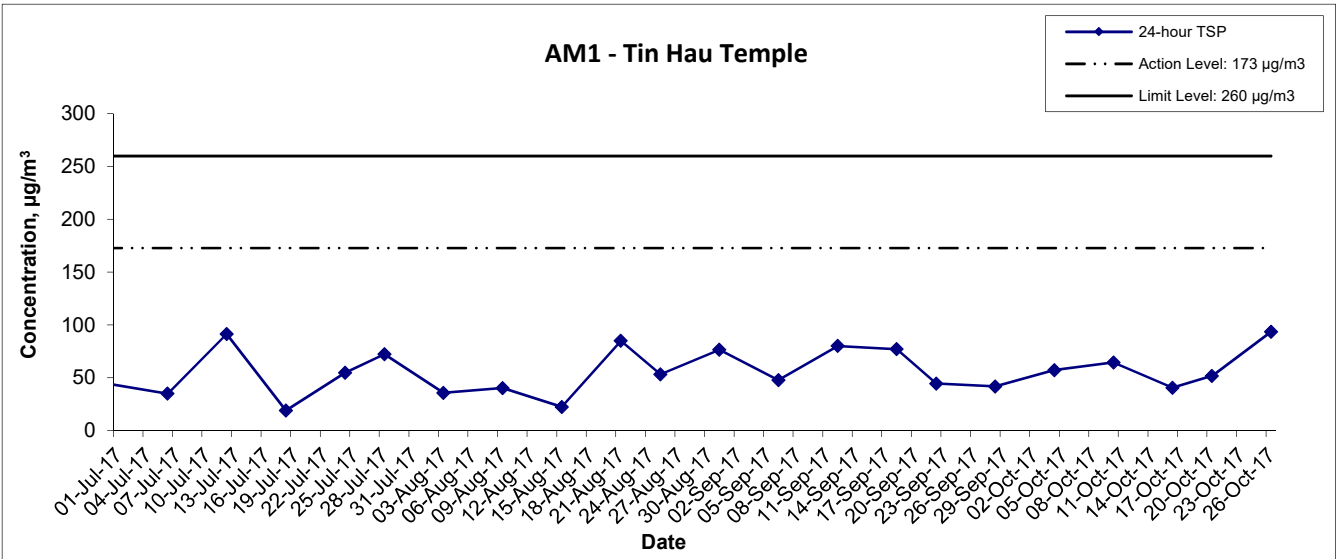

| | | | |
|--|----------------|------------------------|--|
| Title Agreement No. CE/59/2015 (EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction Graphical Presentation of 24-hour TSP Monitoring Results | Scale N.T.S | Project No. MA16034 | |
| | Date Oct 17 | Appendix F | |

24-hr TSP Concentration Levels

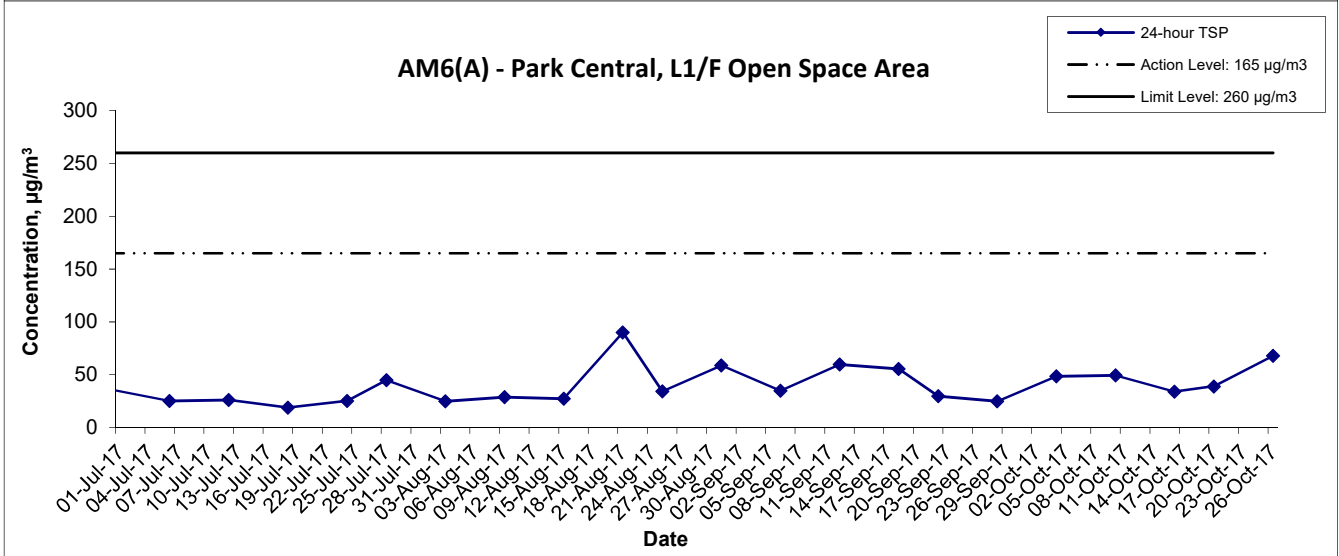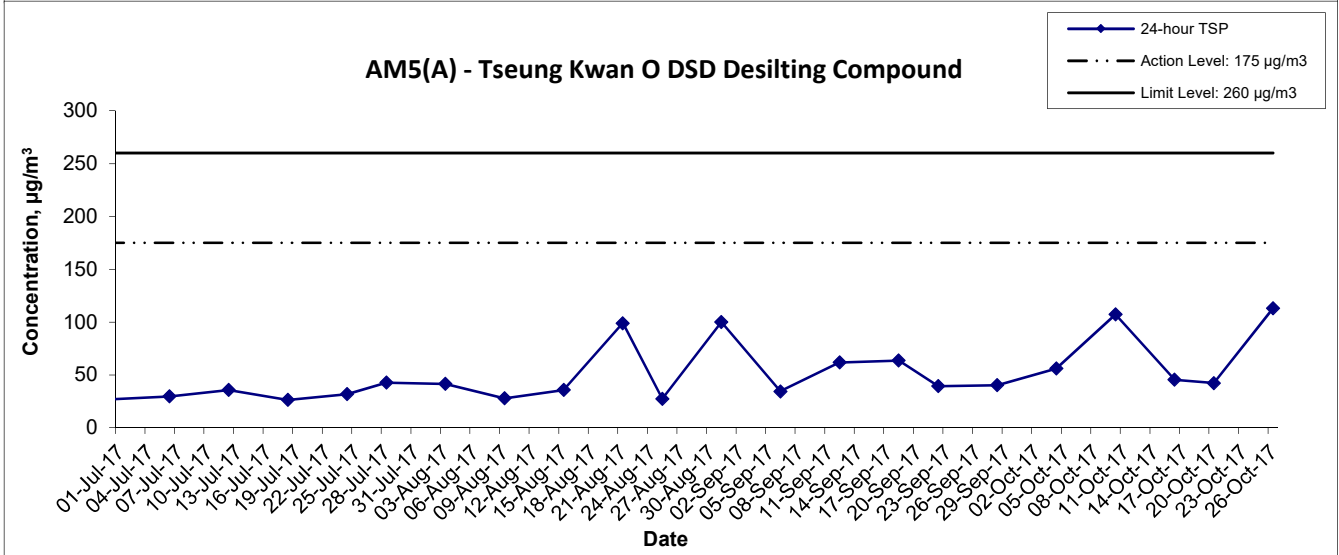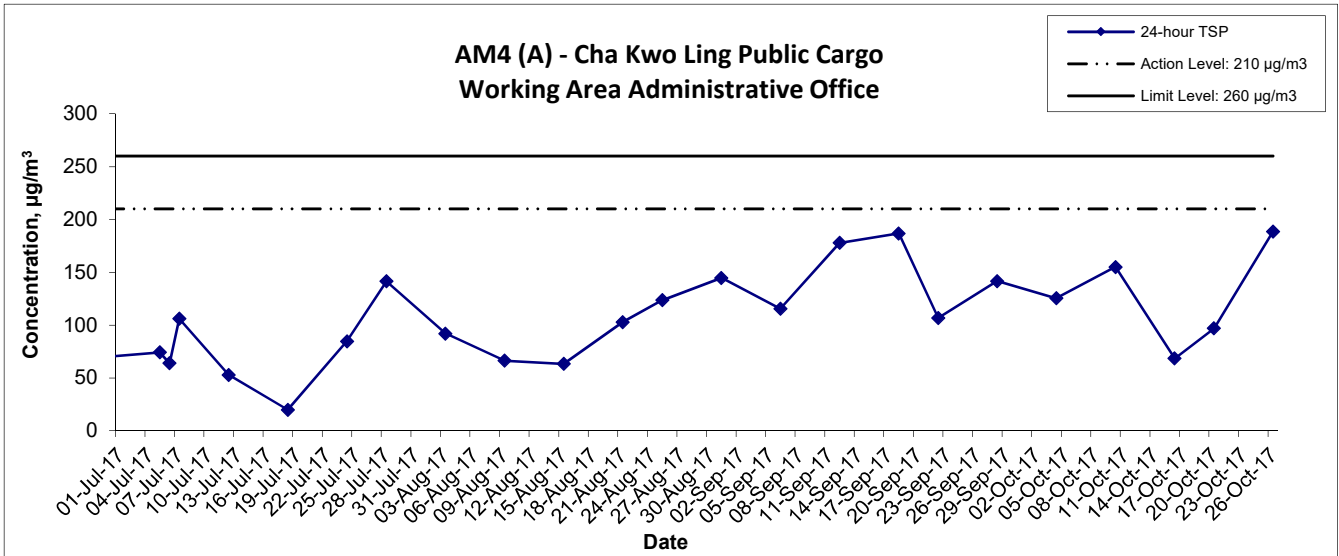

| | | | |
|--|----------------|------------------------|-----------------|
| Title Agreement No. CE/59/2015 (EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction Graphical Presentation of 24-hour TSP Monitoring Results | Scale N.T.S | Project No. MA16034 | CINOTECH |
| | Date Oct 17 | Appendix F | |

**APPENDIX G
NOISE MONITORING RESULTS AND
GRAPHICAL PRESENTATIONS**

Appendix G - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

| Location CM1 - Nga Lai House, Yau Lai Estate Phase 1, Yau Tong | | | | | | | |
|--|-------|---------|-----------------------|-----------------|-----------------|-----------------|--------------------------|
| Date | Time | Weather | Unit: dB (A) (30-min) | | | | |
| | | | Measured Noise Level | | | Baseline Level | Construction Noise Level |
| | | | L _{eq} | L ₁₀ | L ₉₀ | L _{eq} | L _{eq} |
| 3-Oct-17 | 10:00 | Sunny | 74.2 | 77.0 | 69.7 | 65.5 | 73.6 |
| 12-Oct-17 | 10:30 | Sunny | 76.2 | 79.2 | 70.5 | | 75.8 |
| 12-Oct-17 | 11:00 | Sunny | 75.6 | 78.2 | 71.3 | | 75.2 |
| 13-Oct-17 | 10:40 | Sunny | 74.1 | 76.7 | 70.0 | | 73.5 |
| 17-Oct-17 | 10:10 | Sunny | 74.6 | 76.8 | 70.5 | | 74.0 |
| 18-Oct-17 | 10:20 | Sunny | 75.3 | 78.8 | 71.1 | | 74.8 |
| 24-Oct-17 | 9:10 | Sunny | 73.9 | 76.5 | 69.7 | | 73.2 |
| 27-Oct-17 | 9:00 | Sunny | 72.4 | 74.8 | 67.5 | | 71.4 |
| 30-Oct-17 | 13:20 | Sunny | 74.7 | 78.9 | 70.7 | | 74.1 |

| Location CM2 - Bik Lai House, Yau Lai Estate Phase 1, Yau Tong | | | | | | | |
|--|-------|---------|-----------------------|-----------------|-----------------|-----------------|--------------------------|
| Date | Time | Weather | Unit: dB (A) (30-min) | | | | |
| | | | Measured Noise Level | | | Baseline Level | Construction Noise Level |
| | | | L _{eq} | L ₁₀ | L ₉₀ | L _{eq} | L _{eq} |
| 6-Oct-17 | 13:10 | Sunny | 73.6 | 75.9 | 71.2 | 63.6 | 73.1 |
| 12-Oct-17 | 13:30 | Sunny | 74.8 | 77.1 | 72.3 | | 74.5 |
| 18-Oct-17 | 11:15 | Sunny | 74.9 | 78.1 | 70.5 | | 74.6 |
| 24-Oct-17 | 14:00 | Cloudy | 71.4 | 74.4 | 67.4 | | 70.6 |
| 30-Oct-17 | 14:30 | Sunny | 74.8 | 76.9 | 71.4 | | 74.5 |

| Location CM3 - Block S, Yau Lai Estate Phase 5, Yau Tong | | | | | | | |
|--|-------|---------|-----------------------|-----------------|-----------------|-----------------|--------------------------|
| Date | Time | Weather | Unit: dB (A) (30-min) | | | | |
| | | | Measured Noise Level | | | Baseline Level | Construction Noise Level |
| | | | L _{eq} | L ₁₀ | L ₉₀ | L _{eq} | L _{eq} |
| 3-Oct-17 | 9:00 | Sunny | 73.7 | 76.8 | 69.9 | 65.6 | 73.0 |
| 12-Oct-17 | 9:00 | Sunny | 69.2 | 72.0 | 57.0 | | 66.7 |
| 17-Oct-17 | 9:05 | Sunny | 73.9 | 76.3 | 69.2 | | 73.2 |
| 24-Oct-17 | 10:10 | Sunny | 73.6 | 75.8 | 70.2 | | 72.9 |

| Location CM4 - Tin Hau Temple, Cha Kwo Ling | | | | | | | |
|---|-------|---------|-----------------------|-----------------|-----------------|-----------------|--------------------------|
| Date | Time | Weather | Unit: dB (A) (30-min) | | | | |
| | | | Measured Noise Level | | | Baseline Level | Construction Noise Level |
| | | | L _{eq} | L ₁₀ | L ₉₀ | L _{eq} | L _{eq} |
| 6-Oct-17 | 9:05 | Sunny | 71.4 | 73.8 | 68.4 | 62.0 | 70.9 |
| 12-Oct-17 | 8:40 | Sunny | 63.3 | 65.1 | 59.4 | | 57.4 |
| 18-Oct-17 | 9:15 | Sunny | 60.3 | 66.1 | 51.3 | | 60.3 Measured ≤ Baseline |
| 24-Oct-17 | 10:30 | Sunny | 58.4 | 59.9 | 52.7 | | 58.4 Measured ≤ Baseline |
| 30-Oct-17 | 13:15 | Sunny | 60.9 | 63.6 | 54.0 | | 60.9 Measured ≤ Baseline |

| Location CM5 - CCC Kei Faat Primary School, Yau Tong | | | | | | | |
|--|-------|---------|-----------------------|-----------------|-----------------|-----------------|--------------------------|
| Date | Time | Weather | Unit: dB (A) (30-min) | | | | |
| | | | Measured Noise Level | | | Baseline Level | Construction Noise Level |
| | | | L _{eq} | L ₁₀ | L ₉₀ | L _{eq} | L _{eq} |
| 3-Oct-17 | 11:00 | Sunny | 69.3 | 73.1 | 66.5 | 68.2 | 62.8 |
| 12-Oct-17 | 10:00 | Sunny | 69.3 | 72.2 | 65.3 | | 62.8 |
| 17-Oct-17 | 11:20 | Sunny | 68.9 | 71.7 | 65.8 | | 60.6 |
| 24-Oct-17 | 11:20 | Sunny | 69.0 | 70.8 | 66.8 | | 61.3 |

Appendix G - Noise Monitoring Results




(0700-1900 hrs on Normal Weekdays)

| Location CM6(A) - Site Boundary of Contract No. NE/2015/02 near Tower 1, Ocean Shores | | | | | | | |
|---|-------|---------|-----------------------|-----------------|-----------------|-----------------|--------------------------|
| Date | Time | Weather | Unit: dB (A) (30-min) | | | | |
| | | | Measured Noise Level | | | Baseline Level | Construction Noise Level |
| | | | L _{eq} | L ₁₀ | L ₉₀ | L _{eq} | L _{eq} |
| 3-Oct-17 | 16:35 | Sunny | 71.9 | 73.2 | 69.4 | 61.9 | 71.4 |
| 13-Oct-17 | 14:15 | Sunny | 62.0 | 64.5 | 56.9 | | 45.6 |
| 19-Oct-17 | 13:20 | Sunny | 65.3 | 67.5 | 60.3 | | 62.6 |
| 25-Oct-17 | 11:00 | Sunny | 69.7 | 71.9 | 66.4 | | 68.9 |
| 31-Oct-17 | 10:04 | Sunny | 72.8 | 74.8 | 66.9 | | 72.4 |

| Location CM7(A) - Site Boundary of Contract No. NE/2015/02 near Tower 7, Ocean Shores | | | | | | | |
|---|-------|---------|-----------------------|-----------------|-----------------|-----------------|--------------------------|
| Date | Time | Weather | Unit: dB (A) (30-min) | | | | |
| | | | Measured Noise Level | | | Baseline Level | Construction Noise Level |
| | | | L _{eq} | L ₁₀ | L ₉₀ | L _{eq} | L _{eq} |
| 3-Oct-17 | 17:25 | Sunny | 72.6 | 74.9 | 69.5 | 58.3 | 72.4 |
| 13-Oct-17 | 13:35 | Sunny | 60.5 | 62.5 | 57.4 | | 56.5 |
| 19-Oct-17 | 14:05 | Sunny | 61.5 | 63.8 | 55.7 | | 58.7 |
| 25-Oct-17 | 10:10 | Sunny | 69.5 | 71.2 | 65.8 | | 69.2 |
| 31-Oct-17 | 10:53 | Sunny | 68.9 | 71.2 | 62.1 | | 68.5 |




| Location CM8(A) - Park Central, L1/F Open Space Area | | | | | | | |
|--|-------|---------|-----------------------|-----------------|-----------------|-----------------|--------------------------|
| Date | Time | Weather | Unit: dB (A) (30-min) | | | | |
| | | | Measured Noise Level | | | Baseline Level | Construction Noise Level |
| | | | L _{eq} | L ₁₀ | L ₉₀ | L _{eq} | L _{eq} |
| 3-Oct-17 | 13:30 | Sunny | 66.2 | 69.3 | 59.1 | 69.1 | 66.2 Measured ≤ Baseline |
| 13-Oct-17 | 9:00 | Sunny | 65.2 | 67.6 | 57.4 | | 65.2 Measured ≤ Baseline |
| 19-Oct-17 | 15:00 | Sunny | 65.9 | 69.8 | 58.9 | | 65.9 Measured ≤ Baseline |
| 25-Oct-17 | 13:20 | Sunny | 66.8 | 69.3 | 63.2 | | 66.8 Measured ≤ Baseline |
| 31-Oct-17 | 13:52 | Sunny | 68.2 | 70.0 | 59.6 | | 68.2 Measured ≤ Baseline |

Noise Levels

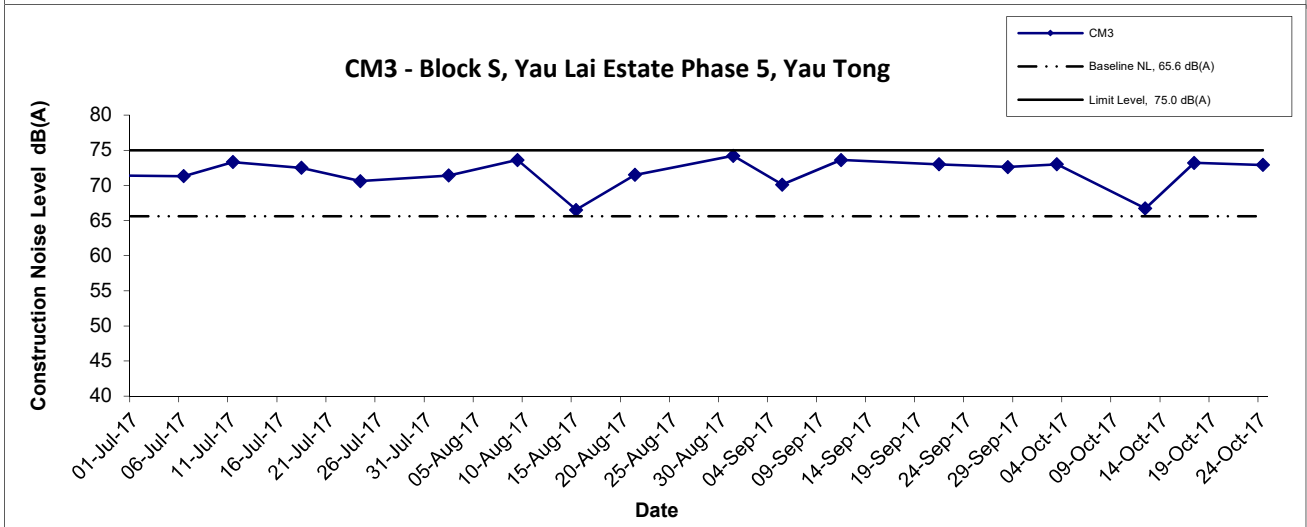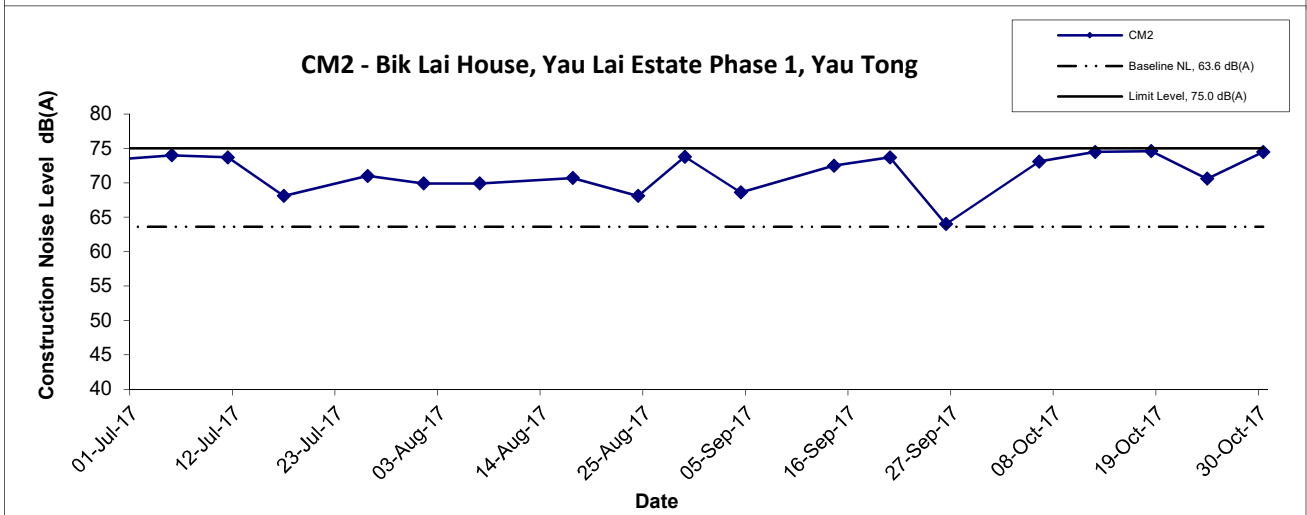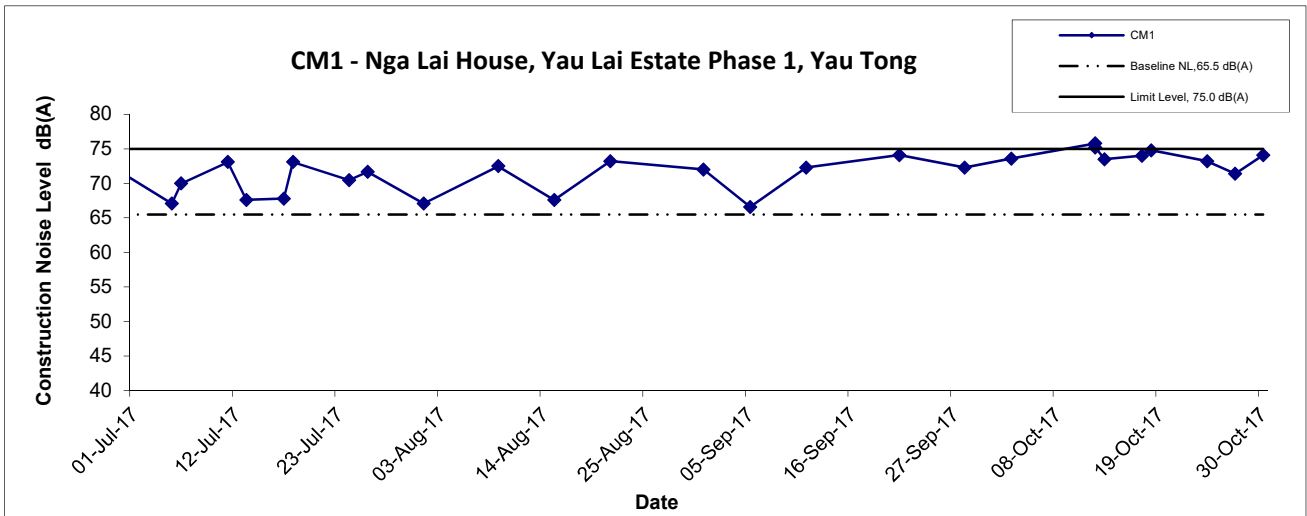



| | | | |
|--|--------------------|------------------------|--|
| Title Agreement No. CE/59/2015 (EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction Graphical Presentation of Construction Noise Monitoring Results | Scale N.T.S | Project No. MA16034 | |
| | Date Oct 17 | Appendix G | |

Noise Levels

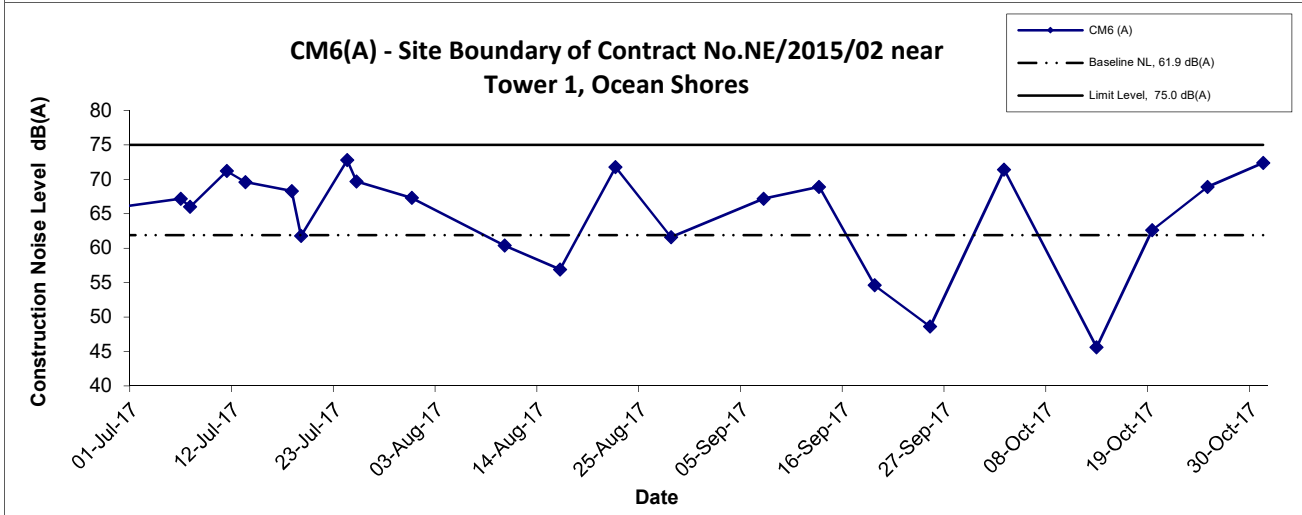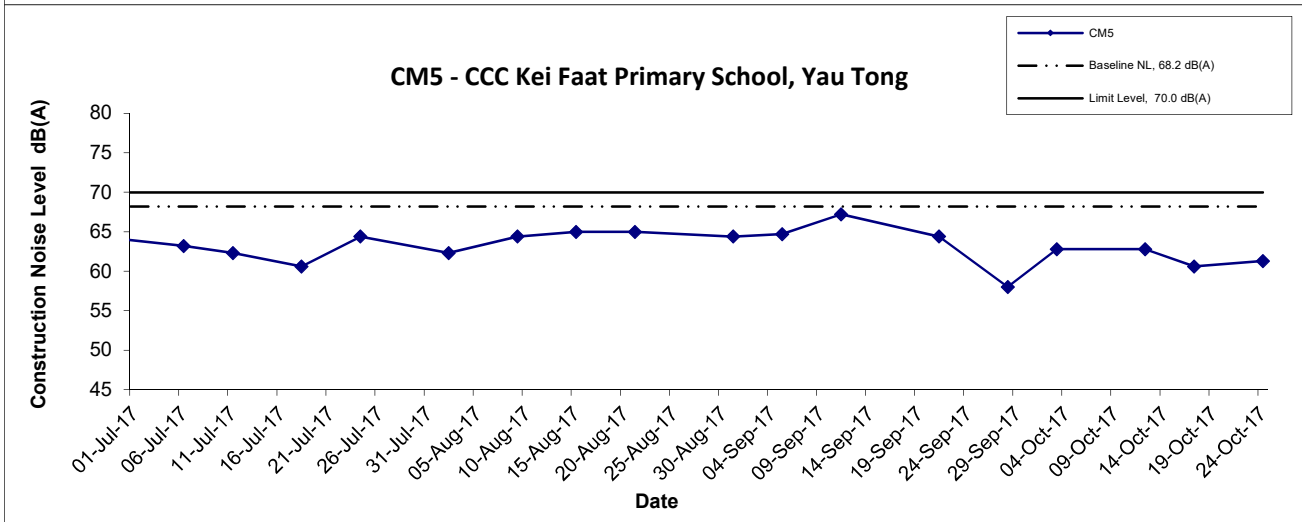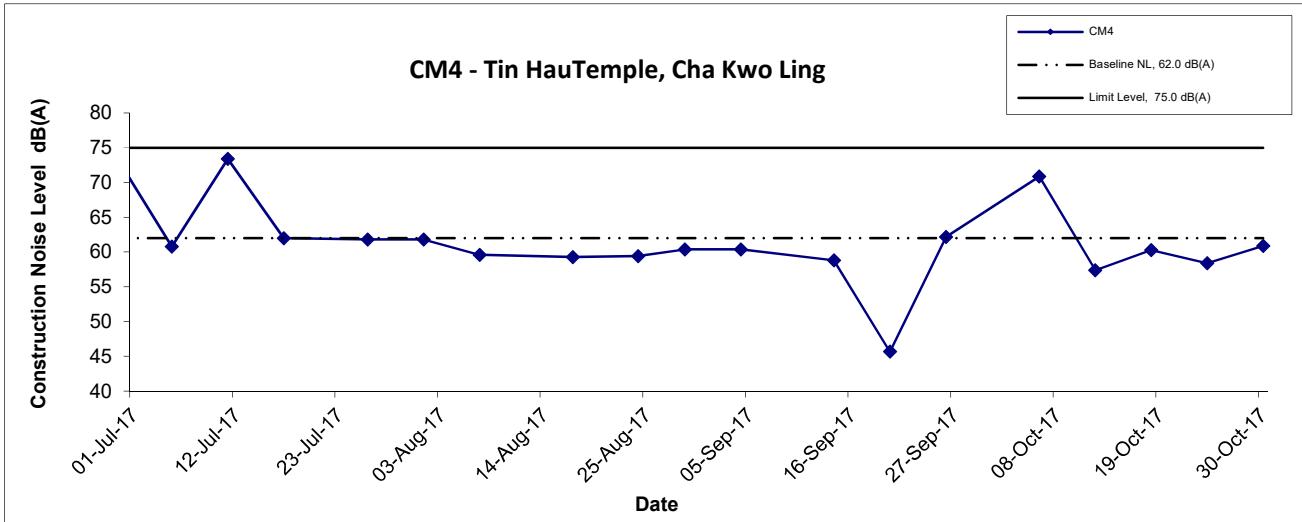

| | | | |
|--|----------------|------------------------|--|
| Title Agreement No. CE/59/2015 (EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction Graphical Presentation of Construction Noise Monitoring Results | Scale N.T.S | Project No. MA16034 | |
| | Date Oct 17 | Appendix G | |

Noise Levels

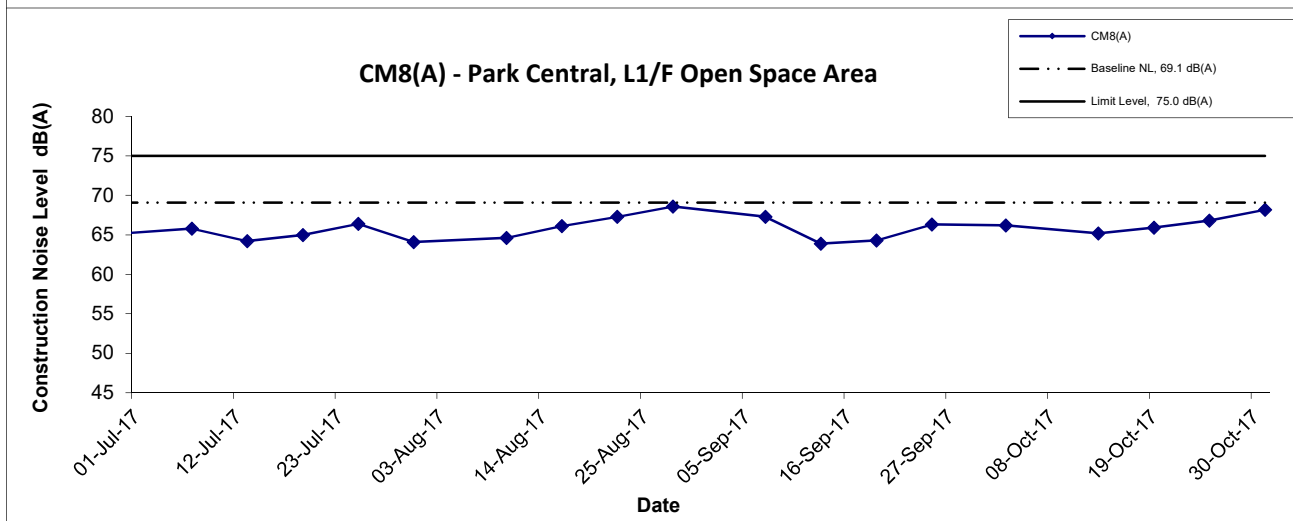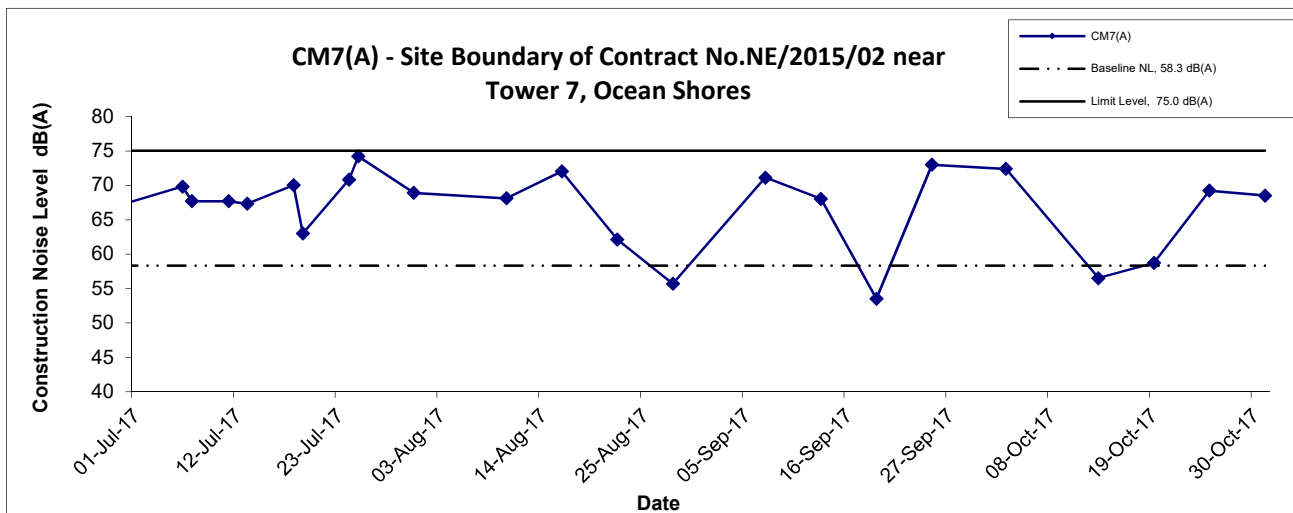

| | | | | | |
|--|-------|--------|----------------|---------|----------|
| Title Agreement No. CE/59/2015 (EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction Graphical Presentation of Construction Noise Monitoring Results | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Date | Oct 17 | Appendix | G | |

**APPENDIX H
GROUNDWATER QUALITY
MONITORING RESULTS AND
GRAPHICAL PRESENTATIONS**

Agreement No. CE/59/2015 (EP)**Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction****Groundwater Quality Monitoring Results at Stream 1**

| Date | Weather Condition | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | Turbidity(NTU) | |
|-----------|-------------------|---------------|-----------|------------------|---------|-------|---------|--------------|---------|-------------------|---------|-------------------------|---------|----------------|---------|
| | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average |
| 12-Oct-17 | Sunny | 09:38 | Middle | 30.7 | 30.7 | 7.9 | 7.9 | 0.1 | 0.1 | 104.4 | 104.2 | 7.8 | 7.8 | 1.9 | 2.0 |
| | | | | 30.6 | | 7.8 | | 0.1 | | 104.0 | | 7.8 | | 2.0 | |
| 26-Oct-17 | Sunny | 15:30 | Middle | 27.6 | 27.6 | 7.6 | 7.6 | 0.1 | 0.1 | 97.6 | 97.0 | 7.8 | 7.8 | 1.3 | 1.4 |
| | | | | 27.5 | | 7.6 | | 0.1 | | 96.3 | | 7.7 | | 1.4 | |

Groundwater Quality Monitoring Results at Stream 2

| Date | Weather Condition | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | Turbidity(NTU) | |
|-----------|-------------------|---------------|-----------|------------------|---------|-------|---------|--------------|---------|-------------------|---------|-------------------------|---------|----------------|---------|
| | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average |
| 12-Oct-17 | Sunny | 09:16 | Middle | 30.8 | 30.8 | 7.9 | 7.9 | 0.1 | 0.1 | 103.9 | 103.9 | 7.7 | 7.7 | 1.9 | 1.9 |
| | | | | 30.8 | | 7.9 | | 0.1 | | 103.9 | | 7.7 | | 1.8 | |
| 26-Oct-17 | Sunny | 16:42 | Middle | 27.1 | 27.1 | 7.6 | 7.6 | 0.3 | 0.3 | 89.9 | 90.5 | 7.8 | 7.8 | 1.3 | 1.4 |
| | | | | 27.1 | | 7.6 | | 0.3 | | 91.1 | | 7.8 | | 1.4 | |

Groundwater Quality Monitoring Results at Stream 3

| Date | Weather Condition | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | Turbidity(NTU) | |
|-----------|-------------------|---------------|-----------|------------------|---------|-------|---------|--------------|---------|-------------------|---------|-------------------------|---------|----------------|---------|
| | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average |
| 12-Oct-17 | Sunny | 09:05 | Middle | 30.1 | 30.5 | 8.0 | 8.0 | 0.1 | 0.1 | 103.1 | 103.7 | 7.8 | 7.8 | 0.8 | 0.8 |
| | | | | 30.8 | | 8.0 | | 0.1 | | 104.2 | | 7.8 | | 0.7 | |
| 26-Oct-17 | Sunny | 16:21 | Middle | 26.9 | 27.1 | 7.6 | 7.6 | 0.1 | 0.1 | 96.1 | 96.2 | 7.8 | 7.8 | 1.3 | 1.3 |
| | | | | 27.2 | | 7.6 | | 0.1 | | 96.3 | | 7.8 | | 1.3 | |

Agreement No. CE/59/2015 (EP)

Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction

Summary of Groundwater Quality Monitoring Results

| Location | Date | Parameters (unit) | | | | | | | | |
|----------|-----------|-------------------|-------------------------|-----------------|-----------|---|----------------|-----------------------|--|---------------------------|
| | | pH | Dissolved Oxygen (mg/L) | Turbidity (NTU) | SS (mg/L) | BOD ₅ (mg O ₂ /L) | TOC (mg-TOC/L) | Total Nitrogen (mg/L) | NH ₃ -N (mg NH ₃ -N/L) | Total Phosphorus (mg-P/L) |
| Stream 1 | 12-Oct-17 | 7.9 | 7.8 | 2.0 | 0.5 | <2 | 3 | 1.4 | <0.05 | <0.05 |
| | 26-Oct-17 | 7.6 | 7.8 | 1.4 | 1.0 | <2 | 3 | 0.6 | <0.05 | <0.05 |
| Stream 2 | 12-Oct-17 | 7.9 | 7.7 | 1.9 | 10 | <2 | 3 | 1.6 | 0.06 | <0.05 |
| | 26-Oct-17 | 7.6 | 7.8 | 1.4 | 1.4 | <2 | 3 | <0.6 | <0.05 | <0.05 |
| Stream 3 | 12-Oct-17 | 8.0 | 7.8 | 0.8 | 0.8 | <2 | 2 | 1.4 | 0.11 | <0.05 |
| | 26-Oct-17 | 7.6 | 7.8 | 1.3 | 0.8 | <2 | 3 | <0.6 | <0.05 | <0.05 |

TEST REPORT

APPLICANT: Cinotech Consultants Limited
1710, Technology Park,
18 On Lai Street,
Shatin, N.T.

| | |
|-----------------|------------|
| Report No.: | 27657 |
| Date of Issue: | 2017-10-23 |
| Date Received: | 2017-10-12 |
| Date Tested: | 2017-10-12 |
| Date Completed: | 2017-10-23 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Sample Description : 3 liquid samples as received from client said to be groundwater
Laboratory No. : 27657
Project No. : MA16034 (Groundwater)
Project Name : Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O –
 Lam Tin Tunnel – Design and Construction
Custody No. : MA16034(Groundwater)/171012
Sampling Date : 2017-10-12

Tests Requested & Methodology:

| Item | Parameters | Ref. Method | Limit of reporting |
|------|---|---|------------------------------|
| 1 | Total Suspended Solids | APHA 17ed 2540 D | *0.5 mg/L |
| 2 | Biochemical Oxygen Demand | APHA 19ed 5210B | 2 mg O ₂ /L |
| 3 | Total Organic Carbon | In-house method SOP020 (Wet Oxidation) | 1 mg-TOC/L |
| 4 | Nitrogen (Total Kjeldahl + nitrate + nitrite) | In-house method SOP063 (FIA) | 0.6 mg N/L |
| 5 | Ammonia | In-house method SOP057 (FIA) | 0.05 mg NH ₃ -N/L |
| 6 | Total Phosphorus | In-house method SOP055 (FIA) | 0.05 mg-P/L |

Results:

| Sample ID | Stream 1 | Stream 2 | Stream 3 |
|--|----------|----------|----------|
| Sampling Depth | S | S | S |
| Sample No. | 27657-1 | 27657-2 | 27657-3 |
| Total Suspended Solids (mg/L) | 0.5 | 10 | 0.8 |
| Biochemical Oxygen Demand (mg O ₂ /L) | <2 | <2 | <2 |
| Total Organic Carbon (mg-TOC/L) | 3 | 3 | 2 |
| Nitrogen (Total Kjeldahl + nitrate + nitrite) (mg N/L) | 1.4 | 1.6 | 1.4 |
| Ammonia (mg NH ₃ -N/L) | <0.05 | 0.06 | 0.11 |
| Total Phosphorus (mg-P/L) | <0.05 | <0.05 | <0.05 |

Remarks: 1) <= less than
 2) S = Surface, M = Middle, B = Bottom
 3) * Limit of Reporting is reported as Detection Limit

*****END OF REPORT*****

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
1710, Technology Park,
18 On Lai Street,
Shatin, N.T.

| | |
|-----------------|------------|
| Report No.: | 27738 |
| Date of Issue: | 2017-11-08 |
| Date Received: | 2017-10-26 |
| Date Tested: | 2017-10-26 |
| Date Completed: | 2017-11-08 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Sample Description : 3 liquid samples as received from client said to be groundwater
Laboratory No. : 27738
Project No. : MA16034 (Groundwater)
Project Name : Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O –
 Lam Tin Tunnel – Design and Construction
Custody No. : MA16034(Groundwater)/171026
Sampling Date : 2017-10-26

Tests Requested & Methodology:

| Item | Parameters | Ref. Method | Limit of reporting |
|------|---|---|------------------------------|
| 1 | Total Suspended Solids | APHA 17ed 2540 D | *0.5 mg/L |
| 2 | Biochemical Oxygen Demand | APHA 19ed 5210B | 2 mg O ₂ /L |
| 3 | Total Organic Carbon | In-house method SOP020 (Wet Oxidation) | 1 mg-TOC/L |
| 4 | Nitrogen (Total Kjeldahl + nitrate + nitrite) | In-house method SOP063 (FIA) | 0.6 mg N/L |
| 5 | Ammonia | In-house method SOP057 (FIA) | 0.05 mg NH ₃ -N/L |
| 6 | Total Phosphorus | In-house method SOP055 (FIA) | 0.05 mg-P/L |

Results:

| Sample ID | Stream 1 | Stream 2 | Stream 3 |
|--|----------|----------|----------|
| Sampling Depth | S | S | S |
| Sample No. | 27738-1 | 27738-2 | 27738-3 |
| Total Suspended Solids (mg/L) | 1.0 | 1.4 | 0.8 |
| Biochemical Oxygen Demand (mg O ₂ /L) | <2 | <2 | <2 |
| Total Organic Carbon (mg-TOC/L) | 3 | 3 | 3 |
| Nitrogen (Total Kjeldahl + nitrate + nitrite) (mg N/L) | 0.6 | <0.6 | <0.6 |
| Ammonia (mg NH ₃ -N/L) | <0.05 | <0.05 | <0.05 |
| Total Phosphorus (mg-P/L) | <0.05 | <0.05 | <0.05 |

Remarks: 1) <= less than
 2) S = Surface, M = Middle, B = Bottom
 3) * Limit of Reporting is reported as Detection Limit


*****END OF REPORT*****

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

pH

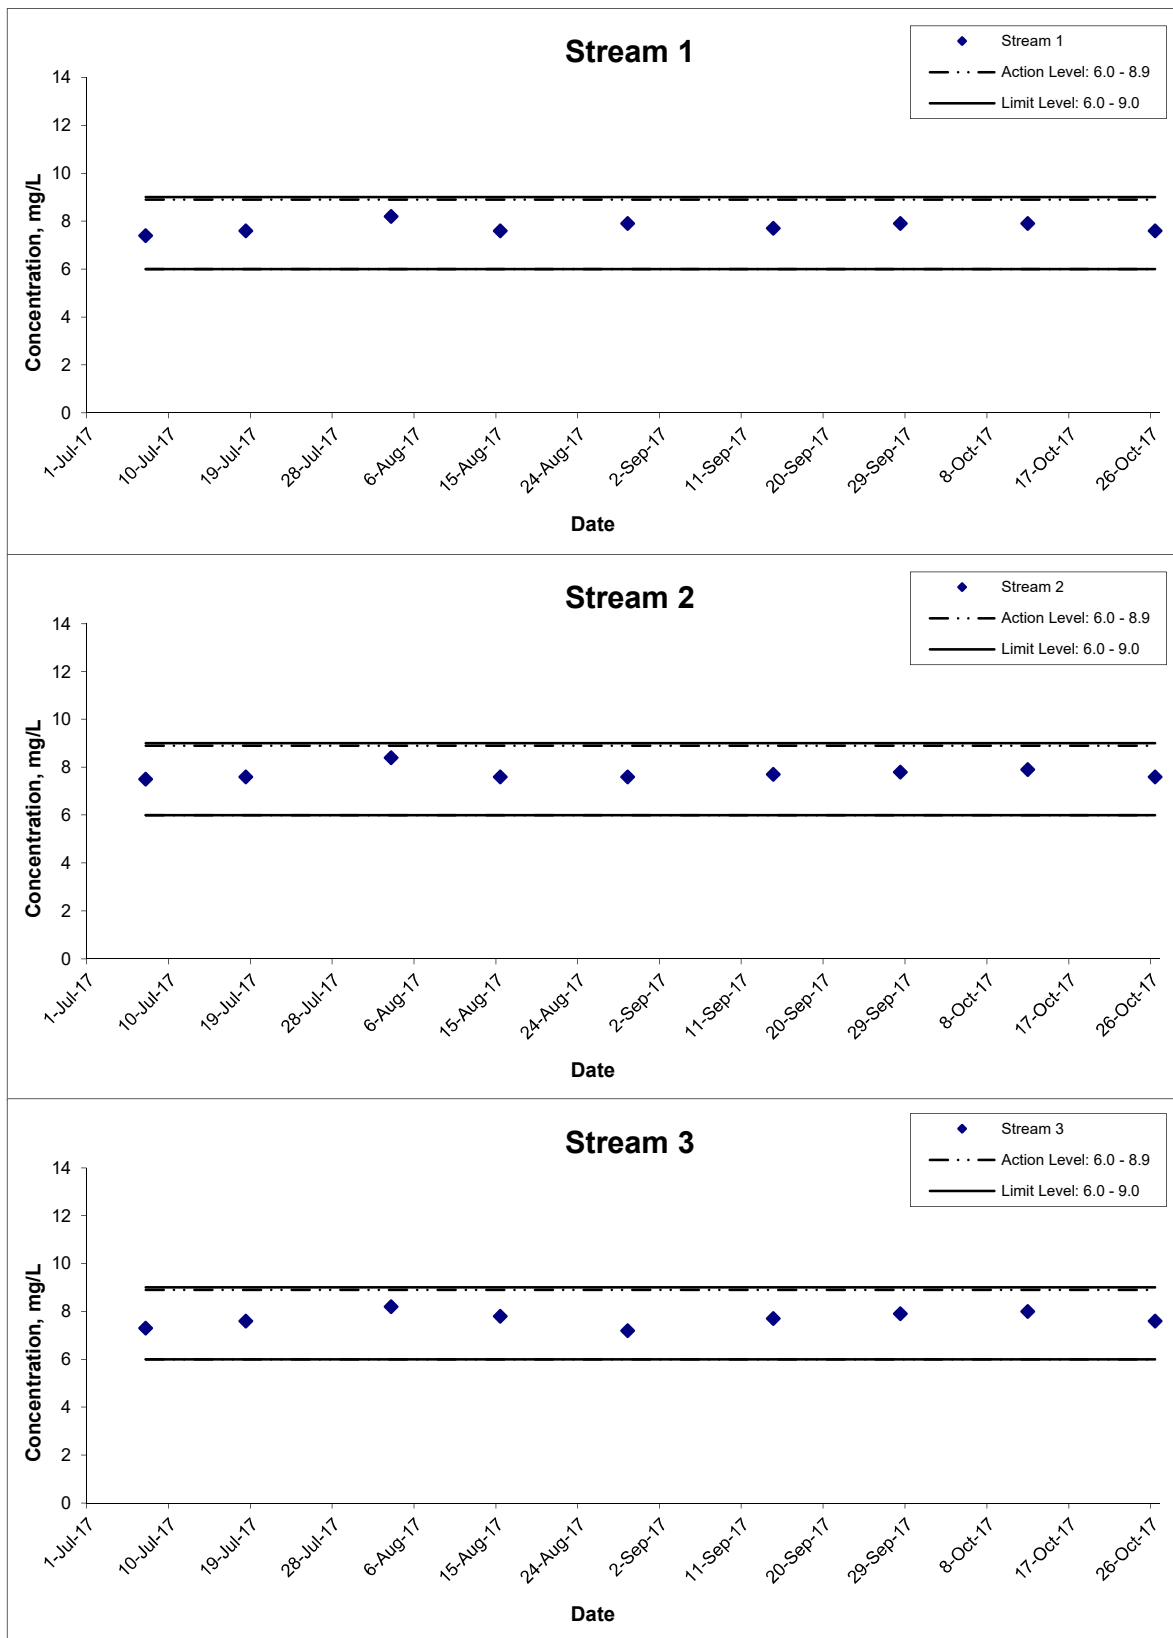


Title Agreement No. CE 59/2015(EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel
 Design and Construction
 Graphical Presentation of Groundwater Quality
 Monitoring Result

Scale N.T.S
 Date Oct 17

Project No. MA16034
 Appendix H



Dissolved Oxygen

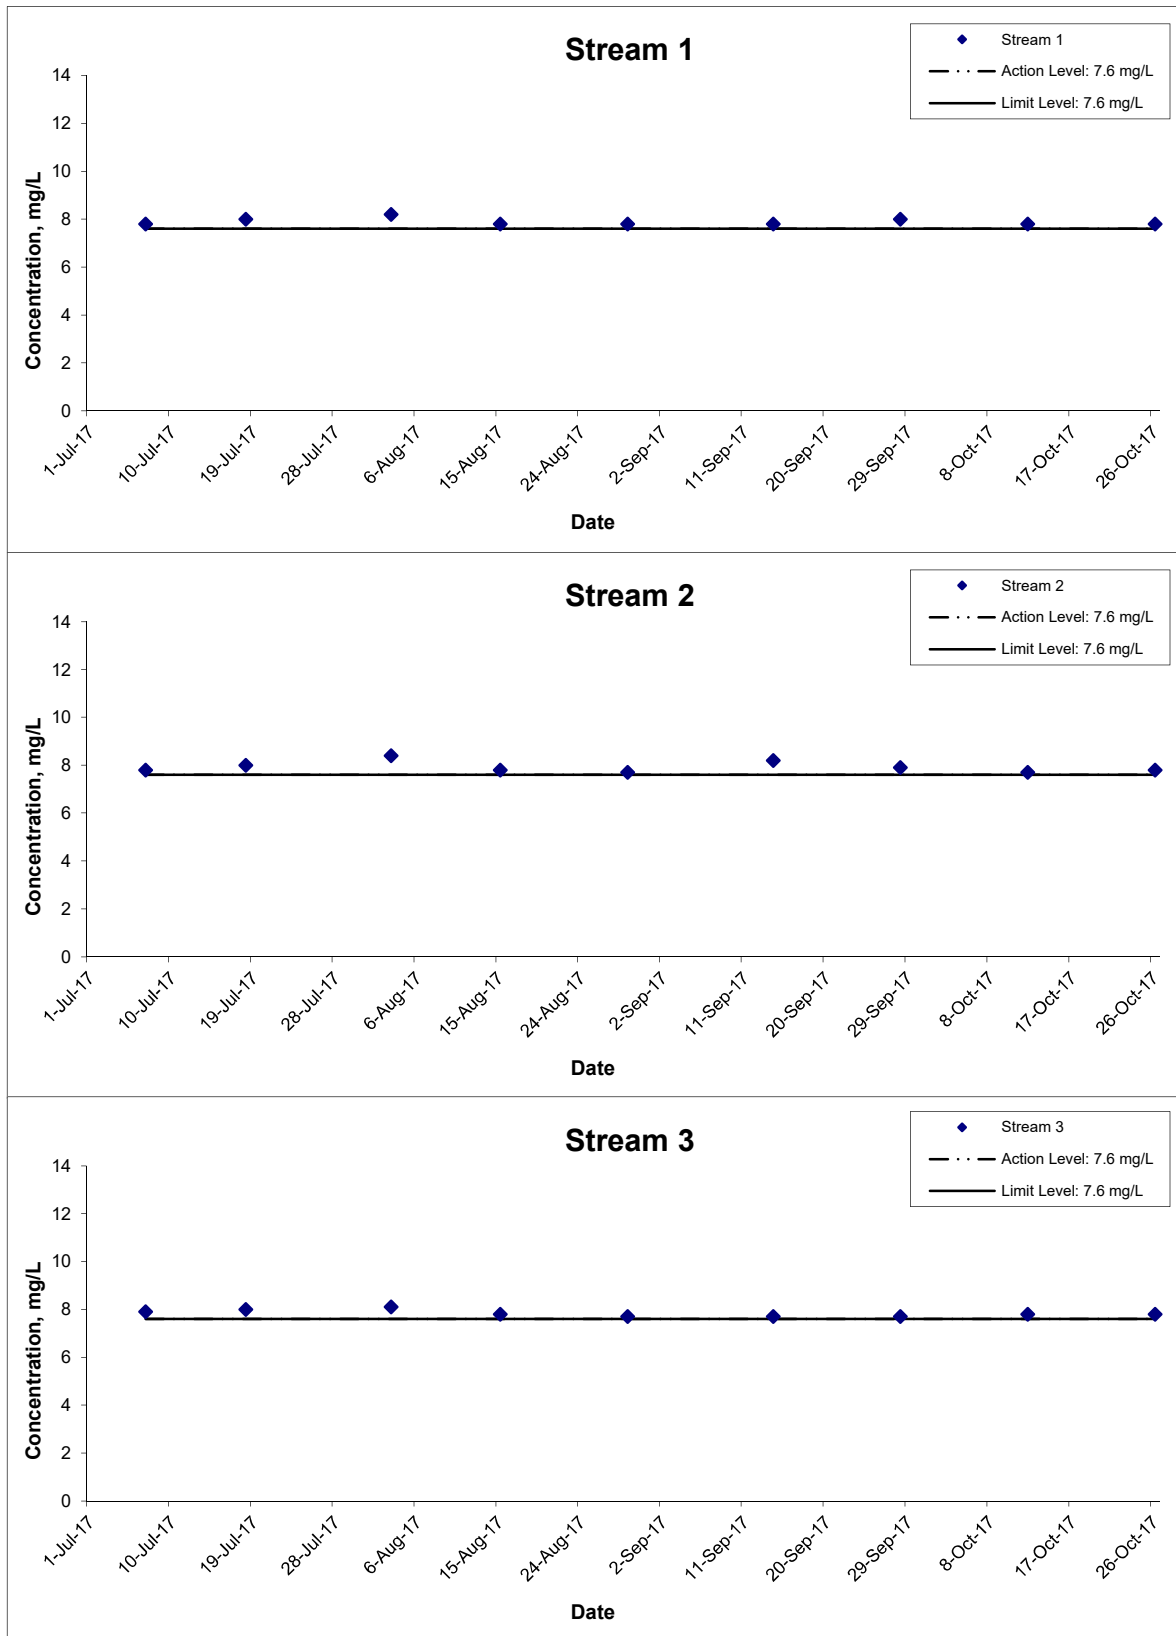


Title Agreement No. CE 59/2015(EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel
 Design and Construction
 Graphical Presentation of Groundwater Quality
 Monitoring Result

Scale N.T.S
 Date Oct 17

Project No. MA16034
 Appendix H



Turbidity

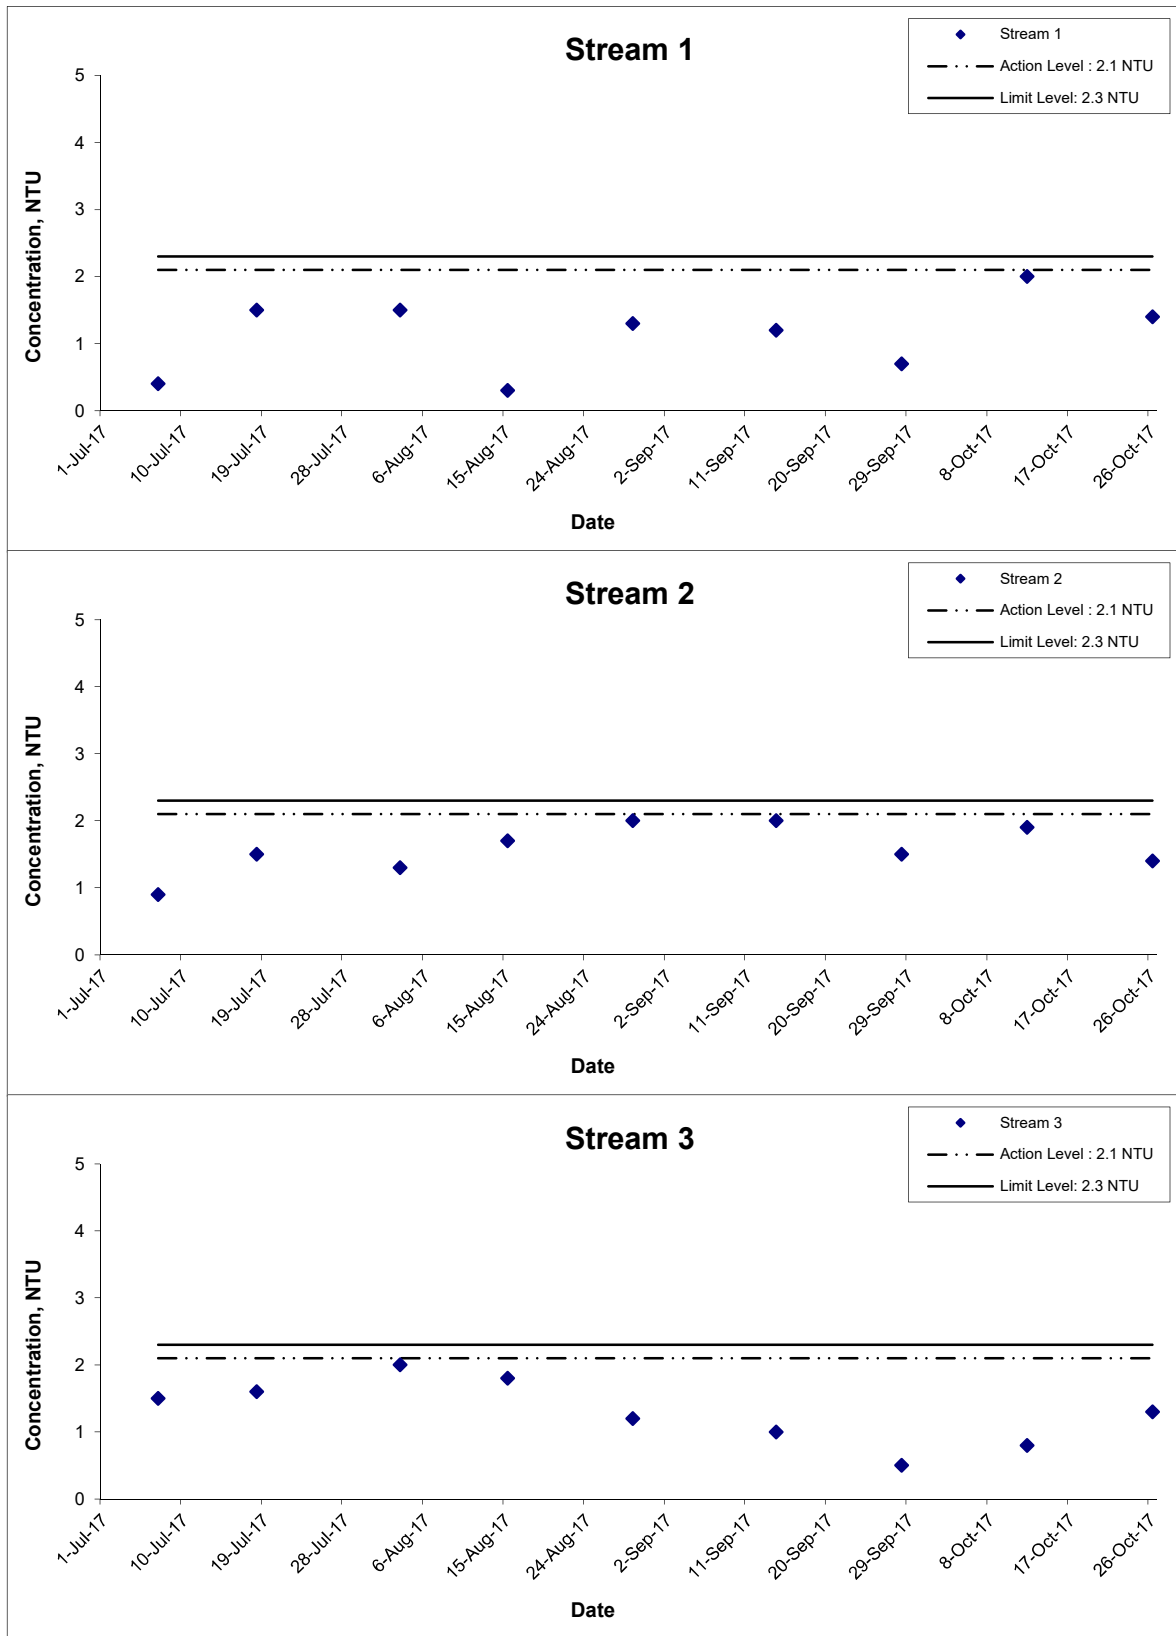


Title Agreement No. CE 59/2015(EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel
 Design and Construction
 Graphical Presentation of Groundwater Quality
 Monitoring Result

Scale N.T.S
 Date Oct 17

Project No. MA16034
 Appendix H



Suspended Solids

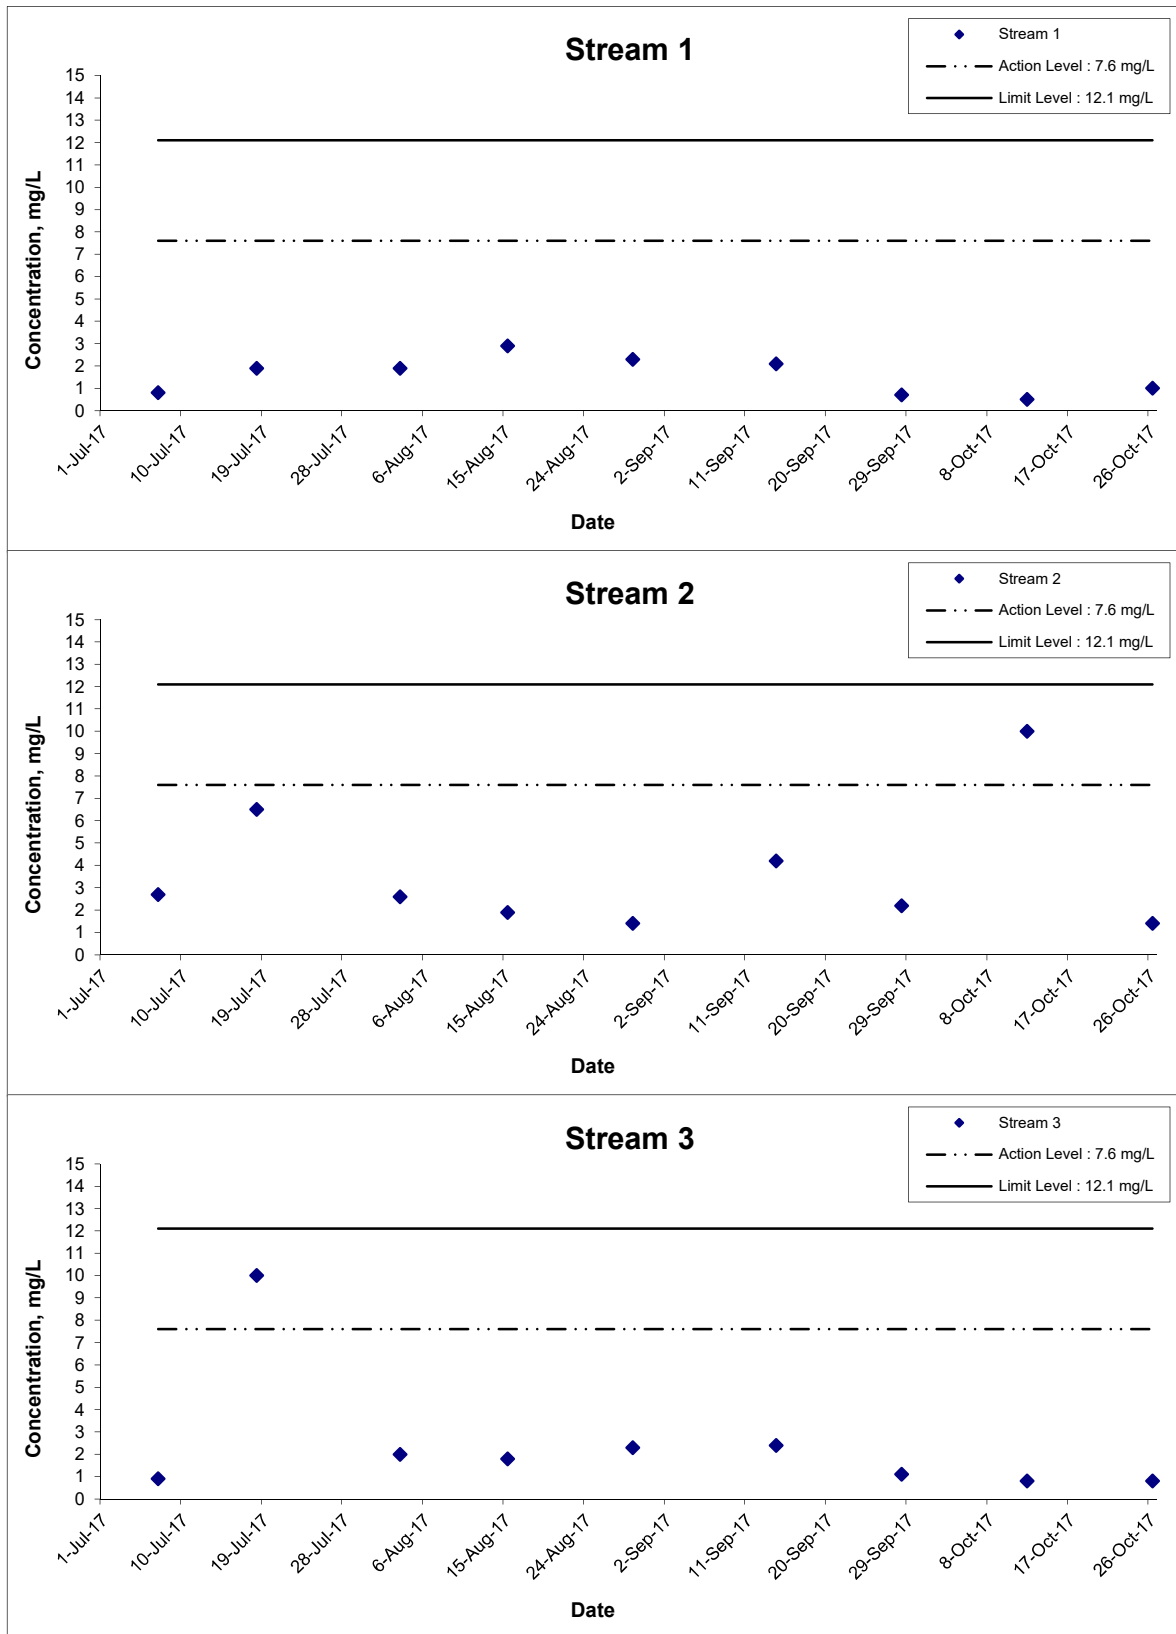


Title Agreement No. CE 59/2015(EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel
 Design and Construction
 Graphical Presentation of Groundwater Quality
 Monitoring Result

Scale N.T.S
 Date Oct 17

Project No. MA16034
 Appendix H




5-day Biochemical Oxygen Demand (BOD₅)

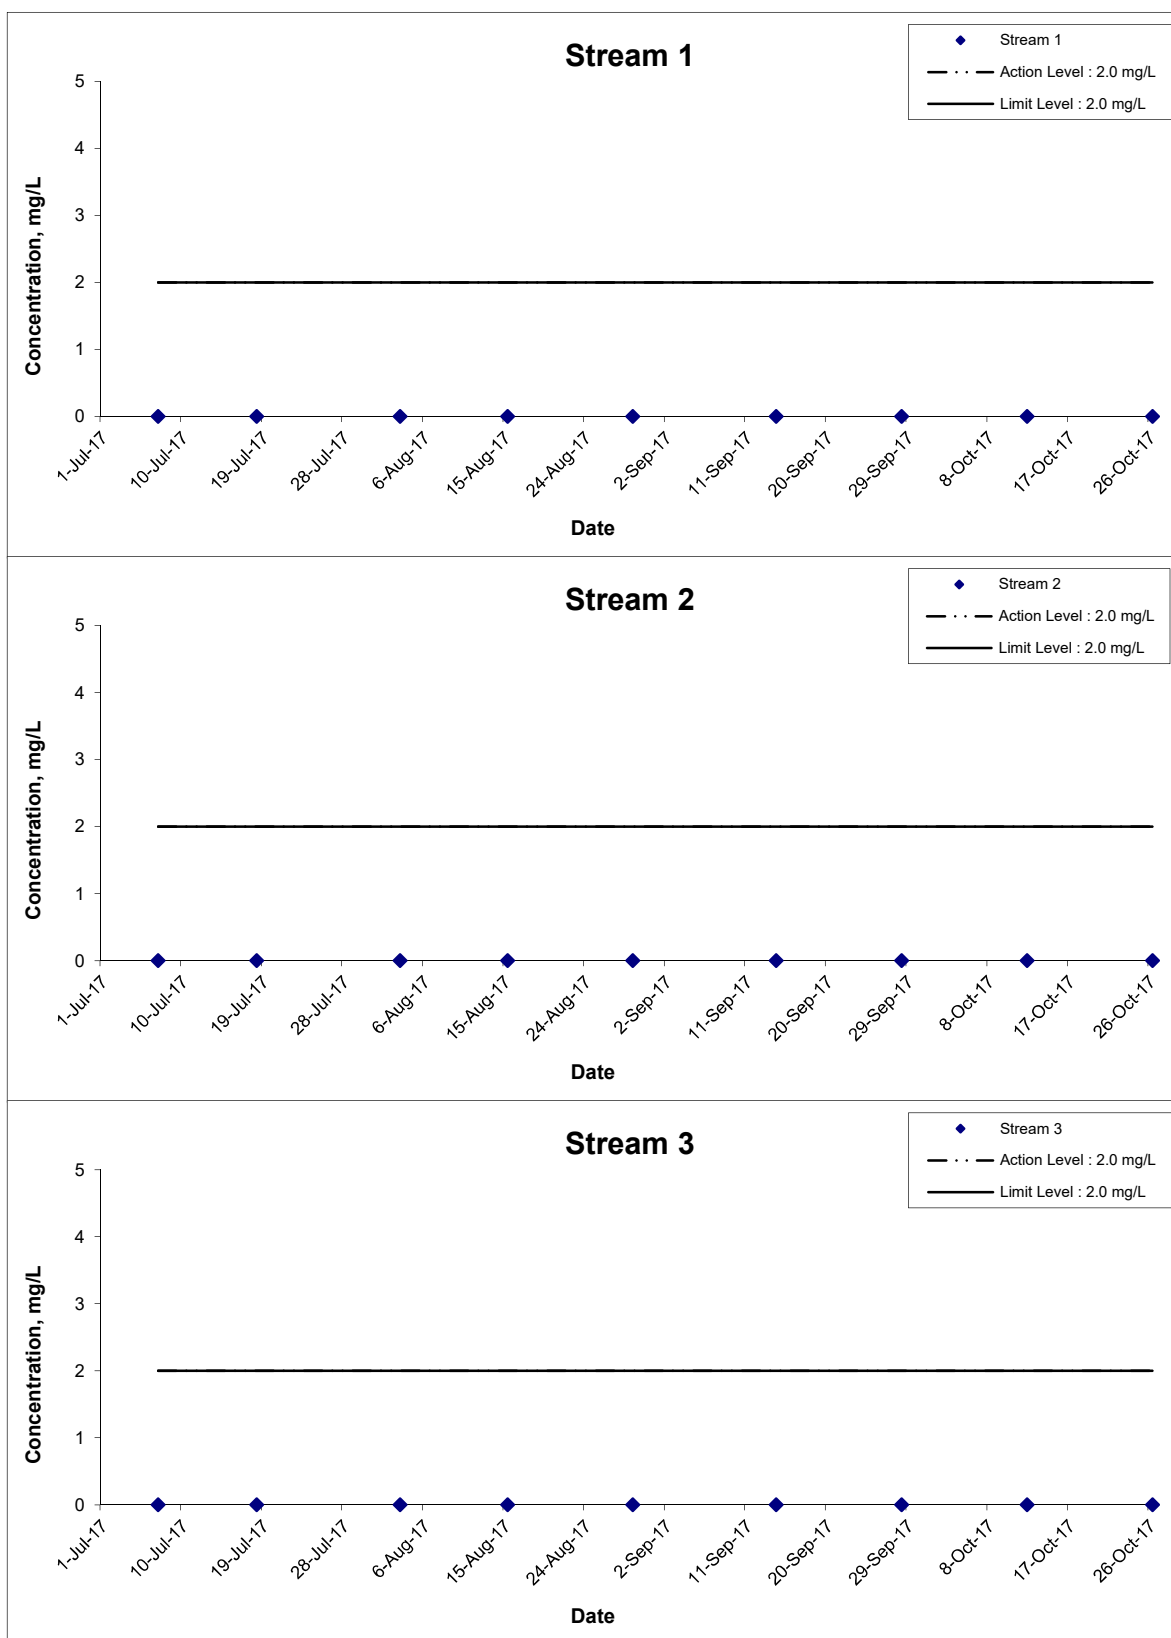

Remarks: The graphical point at zero concentration is presented as <2 mg/L

| | | | | |
|---|-------|--------|------------------------|--|
| Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result | Scale | N.T.S | Project No. MA16034 | |
| | Date | Oct 17 | Appendix H | |

Total Organic Carbon (TOC)

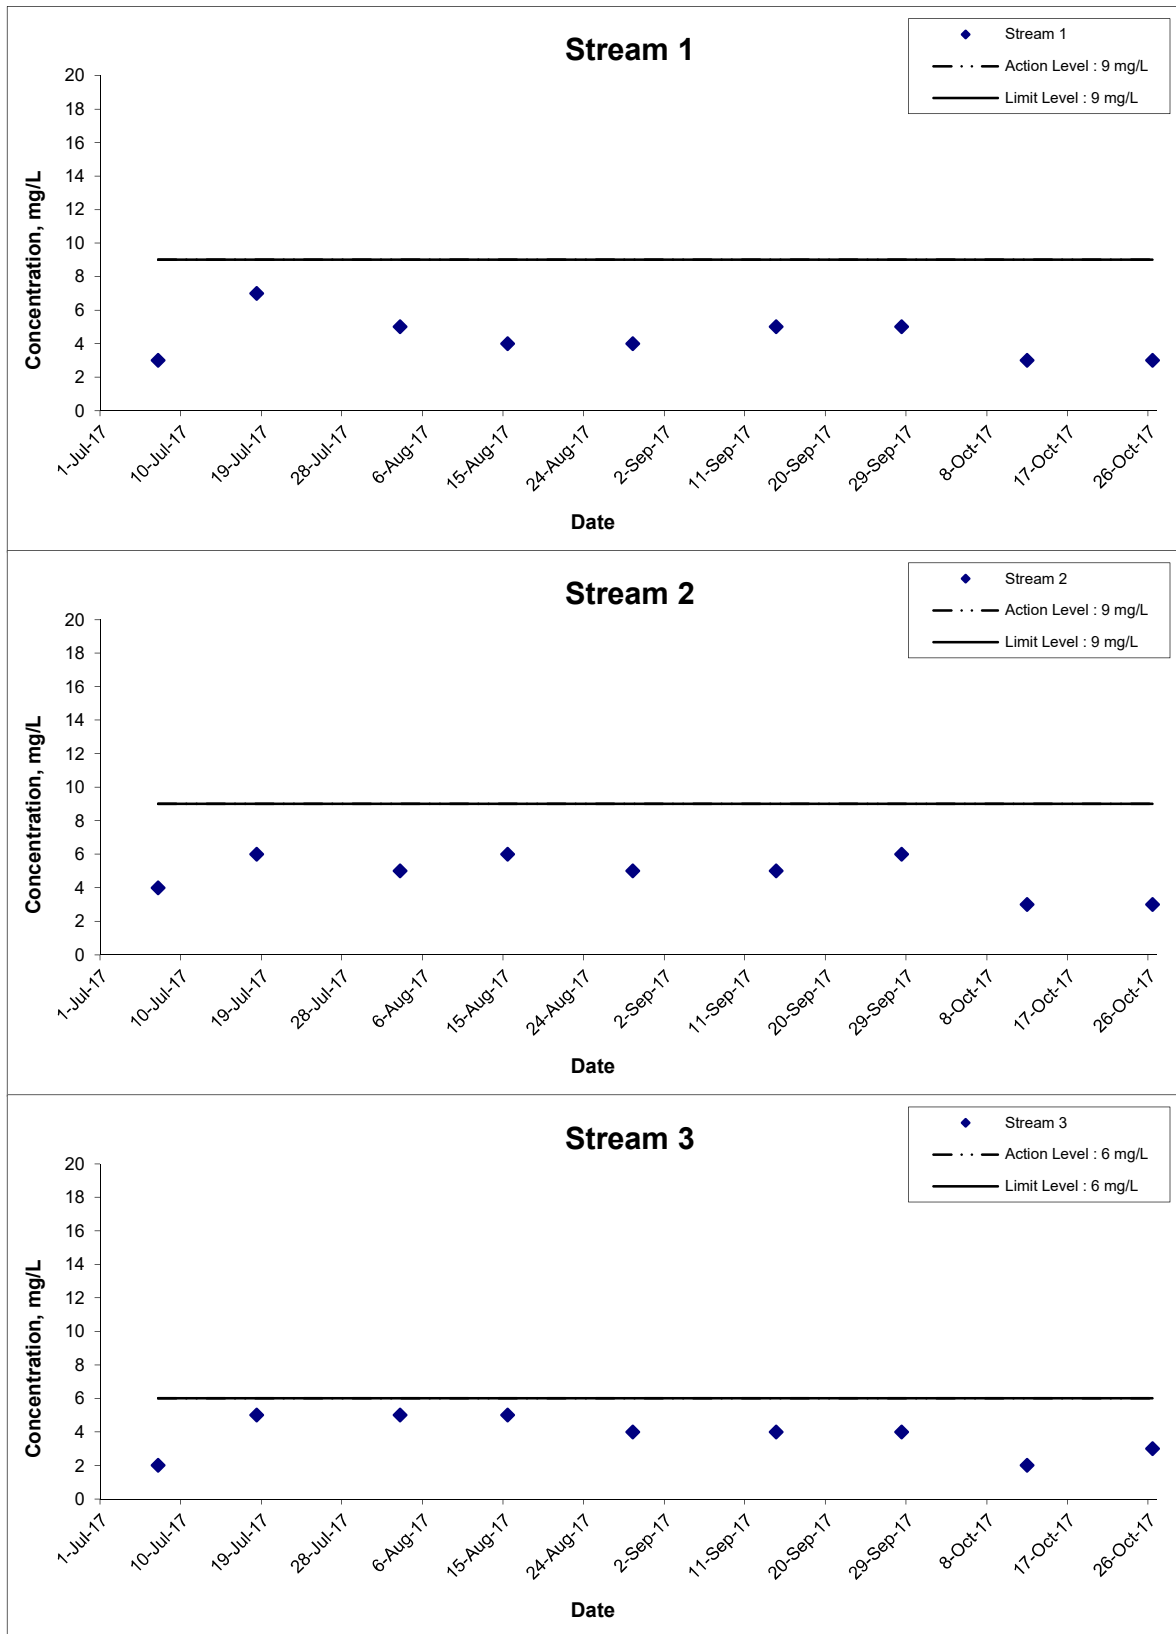


Title Agreement No. CE 59/2015(EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel
 Design and Construction
 Graphical Presentation of Groundwater Quality
 Monitoring Result

Scale N.T.S
 Date Oct 17

Project No. MA16034
 Appendix H




Total Nitrogen

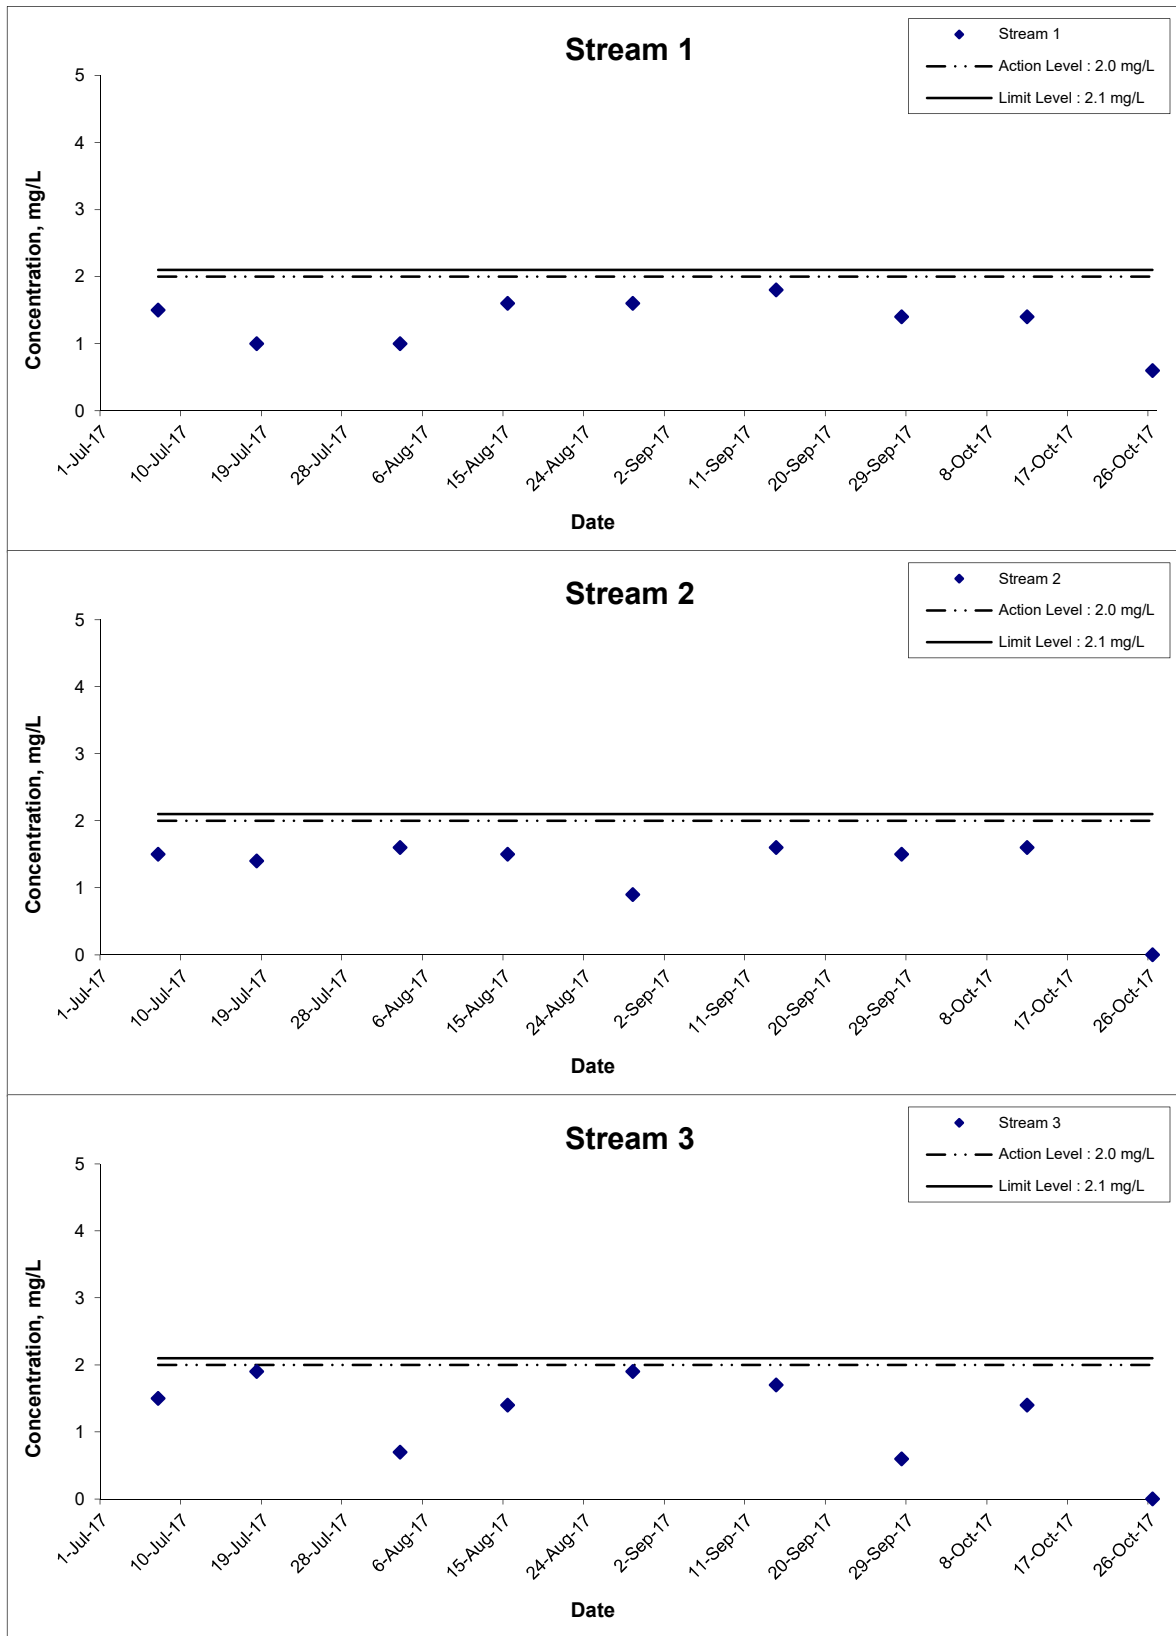

Remarks: The graphical point at zero concentration is presented as <0.6 mg/L

| | | | |
|---|----------------|------------------------|--|
| Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result | Scale N.T.S | Project No. MA16034 | |
| | Date Oct 17 | Appendix H | |


Ammonia-Nitrogen

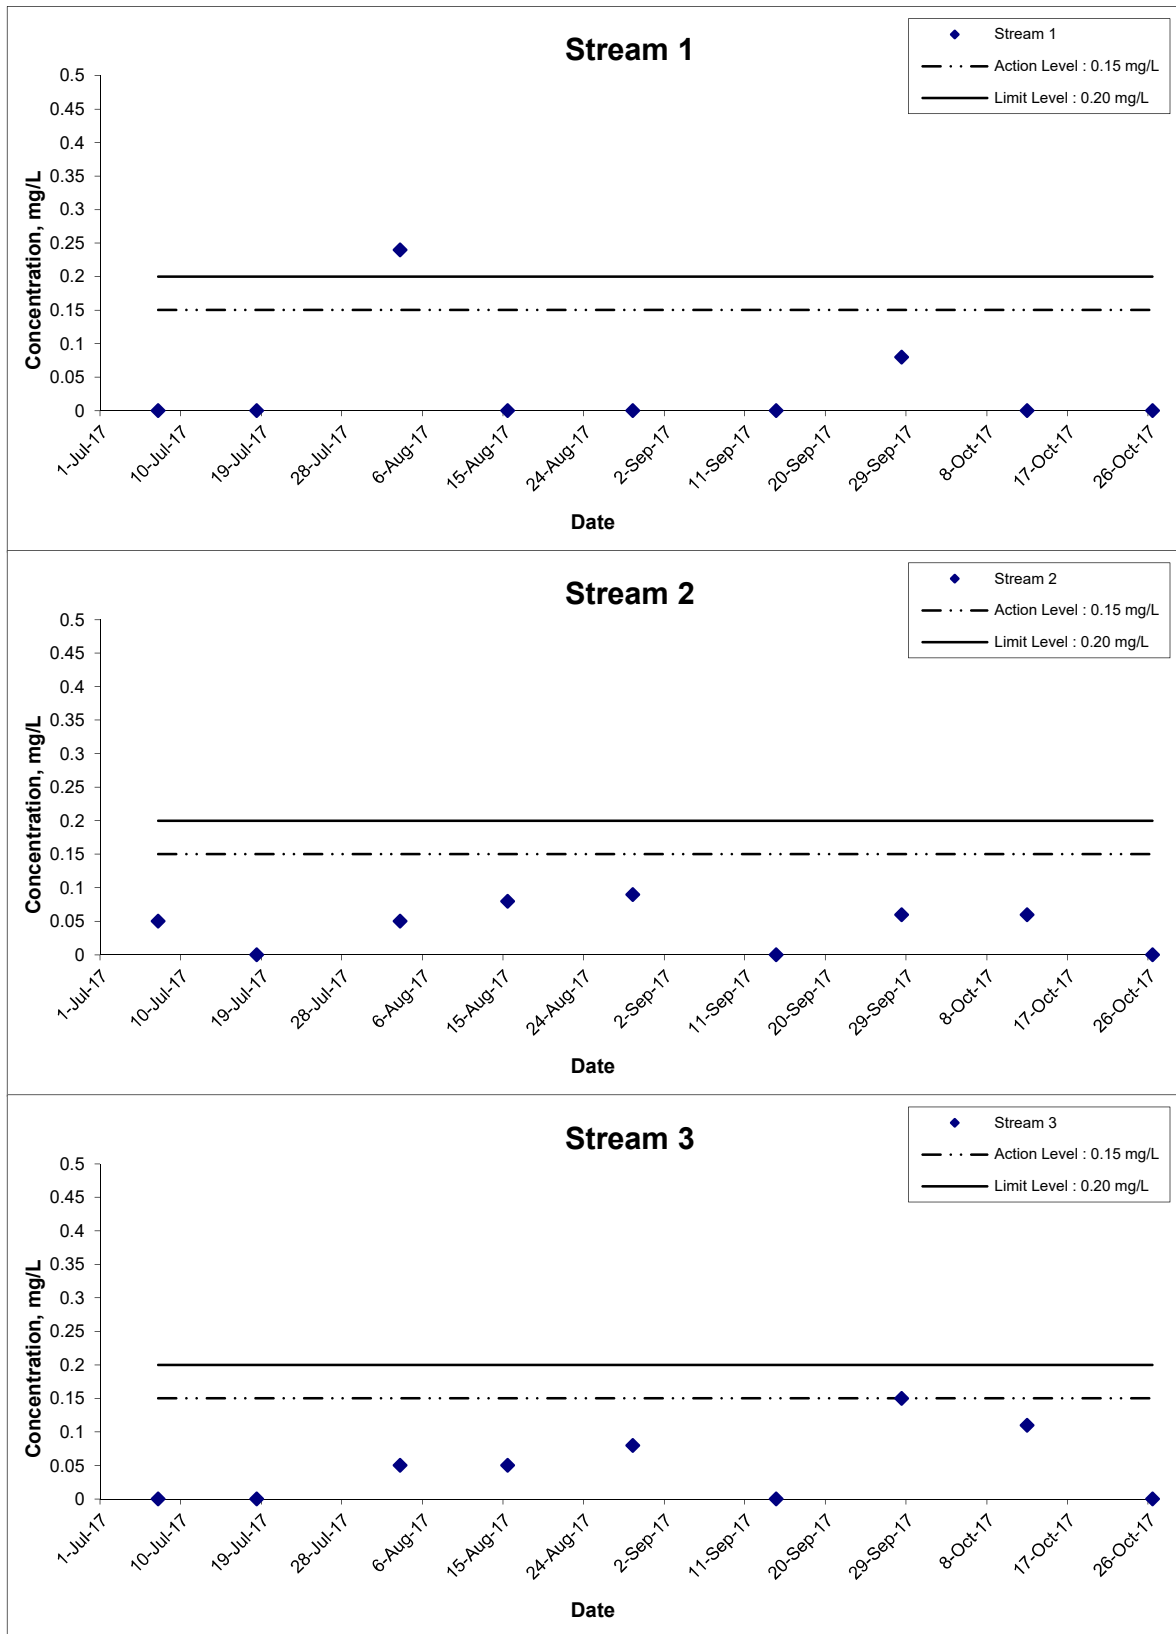

Remarks: The graphical point at zero concentration is presented as <0.05 mg/L

| | | | |
|---|----------------|------------------------|--|
| Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result | Scale N.T.S | Project No. MA16034 | |
| | Date Oct 17 | Appendix H | |

Total Phosphate

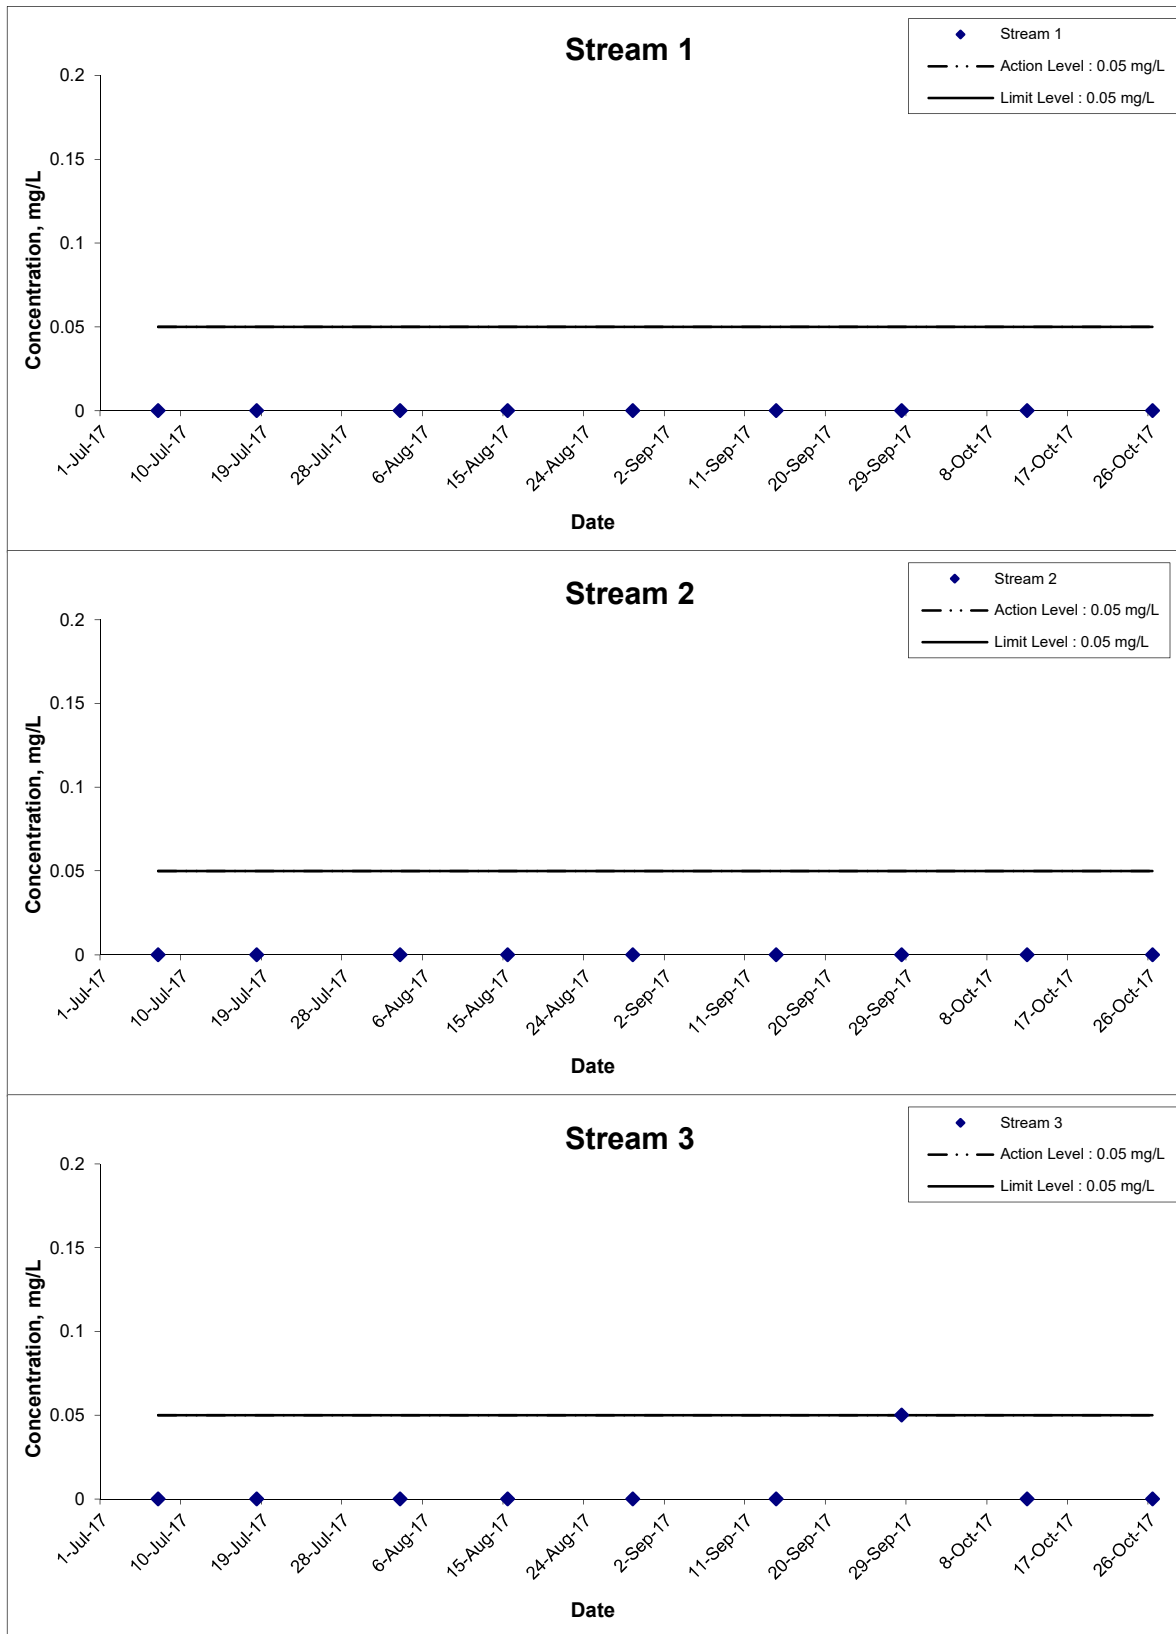

Remarks: The graphical point at zero concentration is presented as <0.05 mg/L

| | | | | | | |
|-------|--|-------|--------|-------------|---------|-----------------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Groundwater Quality Monitoring Result | Date | Oct 17 | Appendix | H | |

**APPENDIX I
MARINE WATER QUALITY
MONITORING RESULTS AND
GRAPHICAL PRESENTATIONS**

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 02 October 2017

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|------------|-----|-----|------------|-----|------------|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | | | | |
| C1 | Sunny | Moderate | 10:17 | Surface | 1 | 29.6 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.5 31.5 | 31.5 | 91.6 90.2 | 90.9 | 5.9 5.8 | 5.9 | 5.5 | 0.5 0.5 | 0.5 | 2.7 | 4.7 4.8 | 8.0 | 4.8 | 5.3 | | |
| | | | | Middle | 9 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 31.8 31.7 | 31.8 | 78.2 78.3 | 78.3 | 5.0 5.0 | 5.0 | | | | | 1.5 1.4 | | | | 1.5 | 7.9 8.1 |
| | | | | Bottom | 17 | 29.4 29.4 | 29.4 | 8.2 8.3 | 8.3 | 32.3 32.3 | 32.3 | 70.0 70.7 | 70.4 | 4.5 4.5 | 4.5 | | | | | 6.6 5.5 | | | | 6.1 | 3.1 3.0 |
| C2 | Sunny | Moderate | 09:12 | Surface | 1 | 29.4 29.4 | 29.4 | 8.2 8.2 | 8.2 | 31.4 31.5 | 31.5 | 83.6 82.6 | 83.1 | 5.4 5.3 | 5.4 | 5.1 | 1.4 1.4 | 1.4 | 4.2 | 4.7 4.5 | 6.9 | 4.6 | 5.5 | | |
| | | | | Middle | 17 | 29.3 29.3 | 29.3 | 8.2 8.2 | 8.2 | 31.9 31.8 | 31.9 | 72.1 74.2 | 73.2 | 4.6 4.8 | 4.7 | | | | | 3.1 2.8 | | | | 3.0 | 6.8 6.9 |
| | | | | Bottom | 33 | 29.3 29.3 | 29.3 | 8.2 8.2 | 8.2 | 32.1 32.1 | 32.1 | 65.9 66.5 | 66.2 | 4.3 4.4 | 4.4 | | | | | 7.8 8.4 | | | | 8.1 | 5.1 5.1 |
| G1 | Sunny | Moderate | 09:44 | Surface | 1 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.3 31.2 | 31.3 | 92.1 89.0 | 90.6 | 5.9 5.7 | 5.8 | 5.8 | 1.5 1.6 | 1.6 | 1.5 | 3.8 3.8 | 5.2 | 5.2 | 4.1 | | |
| | | | | Middle | 4 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.5 31.6 | 31.6 | 90.5 89.4 | 90.0 | 5.8 5.7 | 5.8 | | | | | 0.7 0.6 | | | | 0.7 | 5.2 5.2 |
| | | | | Bottom | 7 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 31.7 31.7 | 31.7 | 80.7 79.8 | 80.3 | 5.2 5.1 | 5.2 | | | | | 2.2 2.2 | | | | 2.2 | 3.4 3.4 |
| G2 | Sunny | Moderate | 09:35 | Surface | 1 | 29.5 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.1 31.3 | 31.2 | 93.7 93.1 | 93.4 | 6.0 6.0 | 6.0 | 5.7 | 0.3 0.3 | 0.3 | 1.3 | 4.8 4.8 | 5.1 | 5.1 | 4.4 | | |
| | | | | Middle | 4.5 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.7 31.7 | 31.7 | 83.2 82.7 | 83.0 | 5.3 5.3 | 5.3 | | | | | 1.0 1.0 | | | | 1.0 | 5.1 5.1 |
| | | | | Bottom | 8 | 29.5 29.5 | 29.5 | 8.2 8.3 | 8.3 | 31.8 31.8 | 31.8 | 73.6 75.9 | 74.8 | 4.7 4.9 | 4.8 | | | | | 2.7 2.5 | | | | 2.6 | 3.4 3.3 |
| G3 | Sunny | Moderate | 09:49 | Surface | 1 | 29.6 29.7 | 29.7 | 8.3 8.2 | 8.3 | 31.1 31.3 | 31.2 | 85.0 73.4 | 79.2 | 5.5 4.7 | 5.1 | 5.2 | 0.5 0.5 | 0.5 | 2.8 | 4.9 4.9 | 8.0 | 8.2 | 5.7 | | |
| | | | | Middle | 4 | 29.6 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.6 31.6 | 31.6 | 81.3 81.4 | 81.4 | 5.2 5.2 | 5.2 | | | | | 2.0 2.2 | | | | 2.1 | 8.3 8.0 |
| | | | | Bottom | 7 | 29.5 29.5 | 29.5 | 8.2 8.3 | 8.3 | 31.7 31.7 | 31.7 | 74.3 75.7 | 75.0 | 4.8 4.9 | 4.9 | | | | | 5.8 5.8 | | | | 5.8 | 4.0 3.9 |
| G4 | Sunny | Moderate | 09:59 | Surface | 1 | 29.9 29.8 | 29.9 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 91.3 90.1 | 90.7 | 5.8 5.8 | 5.8 | 5.8 | 0.4 0.4 | 0.4 | 2.4 | 3.6 3.6 | 6.1 | 6.1 | 4.7 | | |
| | | | | Middle | 4.5 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.6 31.6 | 31.6 | 88.9 88.8 | 88.9 | 5.7 5.7 | 5.7 | | | | | 0.4 0.4 | | | | 0.4 | 6.1 6.1 |
| | | | | Bottom | 8 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 31.9 31.9 | 31.9 | 73.9 74.5 | 74.2 | 4.7 4.8 | 4.8 | | | | | 6.2 6.3 | | | | 6.3 | 4.2 4.4 |
| M1 | Sunny | Moderate | 09:40 | Surface | 1 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 92.2 87.9 | 90.1 | 5.9 5.6 | 5.8 | 5.8 | 0.3 0.3 | 0.3 | 1.1 | 2.6 2.6 | 5.2 | 5.2 | 4.1 | | |
| | | | | Middle | 3 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.5 31.5 | 31.5 | 88.5 88.7 | 88.6 | 5.7 5.7 | 5.7 | | | | | 0.7 0.6 | | | | 0.7 | 5.2 5.2 |
| | | | | Bottom | 5 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.6 31.6 | 31.6 | 80.2 79.8 | 80.0 | 5.1 5.1 | 5.1 | | | | | 2.0 2.4 | | | | 2.2 | 4.4 4.3 |
| M2 | Sunny | Moderate | 09:29 | Surface | 1 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.0 30.9 | 31.0 | 93.4 91.8 | 92.6 | 6.0 5.9 | 6.0 | 5.7 | 0.4 0.4 | 0.4 | 2.1 | 4.1 4.6 | 2.9 | 2.9 | 3.7 | | |
| | | | | Middle | 6 | 29.6 29.5 | 29.6 | 8.3 8.3 | 8.3 | 31.7 31.6 | 31.7 | 82.5 84.6 | 83.6 | 5.3 5.4 | 5.4 | | | | | 1.0 0.9 | | | | 1.0 | 2.9 2.9 |
| | | | | Bottom | 11 | 29.4 29.5 | 29.5 | 8.2 8.2 | 8.2 | 32.0 32.0 | 32.0 | 68.2 71.5 | 69.9 | 4.4 4.6 | 4.5 | | | | | 4.8 5.0 | | | | 4.9 | 3.8 3.9 |
| M3 | Sunny | Moderate | 09:54 | Surface | 1 | 29.7 29.7 | 29.7 | 8.2 8.2 | 8.2 | 31.3 31.4 | 31.4 | 80.1 78.0 | 79.1 | 5.1 5.0 | 5.1 | 5.2 | 0.5 0.5 | 0.5 | 1.9 | 3.1 3.0 | 2.8 | 2.8 | 3.4 | | |
| | | | | Middle | 4 | 29.6 29.6 | 29.6 | 8.2 8.3 | 8.3 | 31.6 31.6 | 31.6 | 77.4 82.3 | 79.9 | 5.0 5.3 | 5.2 | | | | | 1.9 1.9 | | | | 1.9 | 2.8 2.8 |
| | | | | Bottom | 7 | 29.5 29.5 | 29.5 | 8.2 8.3 | 8.3 | 31.7 31.7 | 31.7 | 75.8 75.1 | 75.5 | 4.9 4.8 | 4.9 | | | | | 3.2 3.2 | | | | 3.2 | 4.2 4.3 |
| M4 | Sunny | Moderate | 09:23 | Surface | 1 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 30.9 30.9 | 30.9 | 89.6 88.4 | 89.0 | 5.8 5.7 | 5.8 | 5.3 | 0.8 0.7 | 0.8 | 2.8 | 5.2 5.3 | 8.6 | 8.5 | 5.7 | | |
| | | | | Middle | 5 | 29.3 29.4 | 29.4 | 8.2 8.2 | 8.2 | 32.0 31.7 | 31.9 | 72.7 76.4 | 74.6 | 4.7 4.9 | 4.8 | | | | | 3.4 2.8 | | | | 3.1 | 3.3 3.6 |
| | | | | Bottom | 9 | 29.3 29.3 | 29.3 | 8.2 8.2 | 8.2 | 32.1 32.0 | 32.1 | 67.9 69.8 | 68.9 | 4.4 4.5 | 4.5 | | | | | 4.4 4.5 | | | | 4.5 | 4.4 3.5 |
| M5 | Sunny | Moderate | 10:10 | Surface | 1 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.6 31.6 | 31.6 | 90.2 89.4 | 89.8 | 5.8 5.7 | 5.8 | 5.7 | 0.4 0.5 | 0.5 | 0.6 | 5.5 5.4 | 6.0 | 5.9 | 5.6 | | |
| | | | | Middle | 6 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.8 31.7 | 31.8 | 87.7 86.2 | 87.0 | 5.6 5.5 | 5.6 | | | | | 0.7 0.8 | | | | 0.8 | 5.8 6.0 |
| | | | | Bottom | 11 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.8 31.8 | 31.8 | 88.0 87.0 | 87.5 | 5.6 5.6 | 5.6 | | | | | 0.5 0.6 | | | | 0.6 | 5.6 5.4 |
| M6 | Sunny | Moderate | 10:05 | Surface | - | - | - | - | - | - | - | - | - | - | 5.2 | - | - | 6.8 | - | 3.7 | 3.7 | 3.7 | | | |
| | | | | Middle | 2.2 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.7 31.7 | 31.7 | 75.8 75.5 | 75.7 | 5.2 5.2 | | | | | 5.2 | | | | 6.7 6.9 | 6.8 | 3.7 3.7 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | | | | | - | | | | - | - | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 2 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|--|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 9.7 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 10.5 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.5 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.0 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.5 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.0 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.1 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 02 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|--------------|------|-------------------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 16:59 | Surface | 1 | 29.7 29.7 | 29.7 | 8.2 8.2 | 8.2 | 31.4 31.3 | 31.4 | 84.0 83.1 | 83.6 | 5.4 5.3 | 5.4 | 5.4 | 1.0 0.9 | 1.0 | 4.1 | 4.6 4.6 | 4.6 | 4.1 |
| | | | | Middle | 9 | 29.7 29.6 | 29.7 | 8.3 8.3 | 8.3 | 32.2 32.2 | 32.2 | 85.4 82.8 | 84.1 | 5.4 5.3 | 5.4 | | 1.1 1.2 | 1.2 | | 3.4 3.4 | 3.4 | |
| | | | | Bottom | 17 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 32.4 32.4 | 32.4 | 82.0 80.5 | 81.3 | 5.2 5.1 | 5.2 | | 9.4 10.6 | 10.0 | | 4.3 4.3 | 4.3 | |
| C2 | Sunny | Moderate | 15:54 | Surface | 1 | 30.1 30.2 | 30.2 | 8.2 8.2 | 8.2 | 31.6 31.1 | 31.4 | 89.9 89.6 | 89.8 | 5.7 5.7 | 5.7 | 5.7 | 0.6 0.5 | 0.6 | 1.3 | 3.3 3.2 | 3.3 | 4.1 |
| | | | | Middle | 12 | 29.5 30.0 | 29.8 | 8.2 8.2 | 8.2 | 31.7 31.5 | 31.6 | 77.7 87.4 | 82.6 | 5.6 5.6 | 5.6 | | 1.7 1.8 | 1.8 | | 4.3 4.4 | 4.4 | |
| | | | | Bottom | 23 | 29.4 29.4 | 29.4 | 8.2 8.2 | 8.2 | 32.1 32.0 | 32.1 | 71.5 71.8 | 71.7 | 4.6 4.6 | 4.6 | | 1.6 1.6 | 1.6 | | 4.7 4.5 | 4.6 | |
| G1 | Sunny | Moderate | 16:26 | Surface | 1 | 30.5 30.5 | 30.5 | 8.2 8.3 | 8.3 | 31.2 31.3 | 31.3 | 90.9 91.9 | 91.4 | 5.8 5.8 | 5.8 | 5.7 | 0.4 0.4 | 0.4 | 0.9 | 4.6 4.5 | 4.6 | 4.8 |
| | | | | Middle | 3.5 | 30.0 30.0 | 30.0 | 8.3 8.3 | 8.3 | 31.5 31.5 | 31.5 | 87.4 85.6 | 86.5 | 5.6 5.4 | 5.5 | | 0.6 0.7 | 0.7 | | 5.4 5.1 | 5.3 | |
| | | | | Bottom | 6 | 29.8 29.8 | 29.8 | 8.3 8.3 | 8.3 | 31.8 31.8 | 31.8 | 83.1 84.0 | 83.6 | 5.3 5.4 | 5.4 | | 1.5 1.5 | 1.5 | | 4.6 4.5 | 4.6 | |
| G2 | Sunny | Moderate | 16:15 | Surface | 1 | 30.6 30.6 | 30.6 | 8.2 8.2 | 8.2 | 31.2 31.2 | 31.2 | 91.8 91.5 | 91.7 | 5.8 5.8 | 5.8 | 5.7 | 0.4 0.4 | 0.4 | 0.6 | 4.9 4.9 | 4.9 | 4.3 |
| | | | | Middle | 4 | 30.0 30.0 | 30.0 | 8.2 8.2 | 8.2 | 31.4 31.4 | 31.4 | 86.8 86.4 | 86.6 | 5.5 5.5 | 5.5 | | 0.7 0.6 | 0.7 | | 4.8 4.9 | 4.9 | |
| | | | | Bottom | 7 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.8 31.8 | 31.8 | 85.4 85.0 | 85.2 | 5.5 5.4 | 5.5 | | 0.5 0.6 | 0.6 | | 3.0 3.1 | 3.1 | |
| G3 | Sunny | Moderate | 16:32 | Surface | 1 | 30.0 30.0 | 30.0 | 8.2 8.2 | 8.2 | 31.3 31.2 | 31.3 | 80.9 79.8 | 80.4 | 5.8 5.9 | 5.9 | 5.4 | 1.9 2.0 | 2.0 | 2.3 | 4.2 4.2 | 4.2 | 3.9 |
| | | | | Middle | 3.5 | 29.7 29.7 | 29.7 | 8.2 8.2 | 8.2 | 31.7 31.6 | 31.7 | 74.3 74.7 | 74.5 | 4.8 4.8 | 4.8 | | 2.5 2.3 | 2.4 | | 3.4 3.3 | 3.4 | |
| | | | | Bottom | 6 | 29.6 29.6 | 29.6 | 8.2 8.2 | 8.2 | 31.8 31.8 | 31.8 | 76.6 76.2 | 76.4 | 4.9 4.9 | 4.9 | | 2.4 2.8 | 2.6 | | 4.1 4.2 | 4.2 | |
| G4 | Sunny | Moderate | 16:42 | Surface | 1 | 30.3 30.2 | 30.3 | 8.3 8.3 | 8.3 | 31.4 31.3 | 31.4 | 89.8 88.3 | 89.1 | 5.7 5.6 | 5.7 | 5.5 | 0.4 0.5 | 0.5 | 1.0 | 4.4 4.4 | 4.4 | 4.2 |
| | | | | Middle | 4 | 29.8 29.8 | 29.8 | 8.3 8.3 | 8.3 | 31.6 31.5 | 31.6 | 83.2 82.5 | 82.9 | 5.3 5.3 | 5.3 | | 1.0 0.9 | 1.0 | | 4.0 4.0 | 4.0 | |
| | | | | Bottom | 7 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.8 31.8 | 31.8 | 84.4 84.5 | 84.5 | 5.4 5.4 | 5.4 | | 1.4 1.4 | 1.4 | | 4.0 4.2 | 4.1 | |
| M1 | Sunny | Moderate | 16:21 | Surface | 1 | 30.2 30.4 | 30.3 | 8.2 8.2 | 8.2 | 30.9 31.2 | 31.1 | 85.9 89.5 | 87.7 | 5.5 5.7 | 5.6 | 5.5 | 0.9 0.9 | 0.9 | 1.3 | 3.6 3.6 | 3.6 | 3.8 |
| | | | | Middle | 3 | 30.1 30.0 | 30.1 | 8.2 8.2 | 8.2 | 31.4 31.4 | 31.4 | 85.6 84.3 | 85.0 | 5.4 5.4 | 5.4 | | 1.0 1.0 | 1.0 | | 3.1 3.1 | 3.1 | |
| | | | | Bottom | 5 | 29.7 29.7 | 29.7 | 8.2 8.2 | 8.2 | 31.6 31.6 | 31.6 | 77.5 78.8 | 78.2 | 5.0 5.0 | 5.0 | | 1.9 1.8 | 1.9 | | 4.6 4.7 | 4.7 | |
| M2 | Sunny | Moderate | 16:10 | Surface | 1 | 30.2 30.5 | 30.4 | 8.2 8.2 | 8.2 | 31.3 31.3 | 31.3 | 88.0 90.1 | 89.1 | 5.6 5.7 | 5.7 | 5.6 | 1.8 1.8 | 1.8 | 3.2 | 4.3 4.3 | 4.3 | 4.7 |
| | | | | Middle | 5.5 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.8 31.8 | 31.8 | 84.8 85.5 | 85.3 | 5.4 5.5 | 5.5 | | 0.5 0.5 | 0.5 | | 5.5 5.4 | 5.4 | |
| | | | | Bottom | 10 | 29.6 29.6 | 29.6 | 8.2 8.2 | 8.2 | 32.0 32.0 | 32.0 | 72.3 73.4 | 72.9 | 4.6 4.7 | 4.7 | | 7.4 7.3 | 7.4 | | 4.4 4.4 | 4.4 | |
| M3 | Sunny | Moderate | 16:36 | Surface | 1 | 30.1 30.1 | 30.1 | 8.2 8.2 | 8.2 | 31.0 31.1 | 31.1 | 82.1 80.5 | 81.3 | 5.4 5.5 | 5.5 | 5.2 | 0.7 0.8 | 0.8 | 2.6 | 3.5 3.4 | 3.5 | 4.2 |
| | | | | Middle | 3.5 | 29.6 29.6 | 29.6 | 8.2 8.2 | 8.2 | 31.7 31.7 | 31.7 | 70.1 69.1 | 69.6 | 4.8 4.8 | 4.8 | | 4.1 4.4 | 4.3 | | 5.5 5.3 | 5.4 | |
| | | | | Bottom | 6 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.8 31.8 | 31.8 | 77.3 77.1 | 77.2 | 4.9 4.9 | 4.9 | | 2.8 2.6 | 2.7 | | 3.9 3.5 | 3.7 | |
| M4 | Sunny | Moderate | 16:03 | Surface | 1 | 30.1 30.2 | 30.2 | 8.2 8.2 | 8.2 | 31.3 31.4 | 31.4 | 88.6 88.0 | 88.3 | 5.6 5.6 | 5.6 | 5.5 | 0.5 0.5 | 0.5 | 1.5 | 4.0 3.9 | 4.0 | 3.8 |
| | | | | Middle | 4.5 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.8 31.8 | 31.8 | 83.9 84.1 | 84.0 | 5.4 5.4 | 5.4 | | 0.5 0.5 | 0.5 | | 4.8 4.6 | 4.7 | |
| | | | | Bottom | 8 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 32.1 32.0 | 32.1 | 79.8 82.2 | 81.0 | 5.1 5.2 | 5.2 | | 3.4 3.7 | 3.6 | | 2.7 2.6 | 2.7 | |
| M5 | Sunny | Moderate | 16:53 | Surface | 1 | 29.9 29.9 | 29.9 | 8.2 8.3 | 8.3 | 31.4 31.4 | 31.4 | 85.6 84.5 | 85.1 | 5.5 5.4 | 5.5 | 5.3 | 1.3 1.2 | 1.3 | 5.0 | 2.5 2.6 | 2.6 | 3.1 |
| | | | | Middle | 5.5 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 31.6 31.6 | 31.6 | 80.3 79.7 | 80.0 | 5.1 5.1 | 5.1 | | 2.7 2.8 | 2.8 | | 3.3 3.3 | 3.3 | |
| | | | | Bottom | 10 | 29.5 29.5 | 29.5 | 8.2 8.3 | 8.3 | 32.2 32.3 | 32.3 | 71.6 71.9 | 71.8 | 4.6 4.6 | 4.6 | | 10.7 11.0 | 10.9 | | 3.3 3.3 | 3.3 | |
| M6 | Sunny | Moderate | 16:48 | Surface | - | - | - | - | - | - | - | - | - | - | - | 5.5 | - | - | 0.8 | - | - | 3.4 |
| | | | | Middle | 2.1 | 29.9 29.9 | 29.9 | 8.3 8.3 | 8.3 | 31.6 31.6 | 31.6 | 85.5 85.9 | 85.7 | 5.4 5.5 | 5.5 | | 0.8 0.7 | 0.8 | | 3.4 3.4 | 3.4 | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 2 October 2017 (Mid-Flood Tide)

| <u>Parameter (unit)</u> | <u>Depth</u> | <u>Action Level</u> | <u>Limit Level</u> |
|--|-------------------------------------|--|--|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 12.0 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 13.0 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.5 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.0 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.5 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.0 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.2 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.0 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 04 October 2017**

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|------------|-------------------------|------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | | |
| C1 | Sunny | Moderate | 12:24 | Surface | 1 | 29.7 29.7 | 29.7 | 8.2 8.3 | 8.3 | 31.0 31.0 | 31.0 | 77.8 77.8 | 78.1 | 5.0 5.0 | 5.0 | 5.0 | 5.0 | 1.1 1.3 | 1.2 | 2.2 | 5.5 5.6 | 5.6 | 6.2 |
| | | | | Middle | 9.5 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 32.3 32.3 | 32.3 | 77.3 77.3 | 77.3 | 5.0 5.0 | 5.0 | 5.0 | 5.0 | 1.8 1.8 | 1.8 | | 8.4 8.3 | 8.4 | |
| | | | | Bottom | 18 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 33.4 33.5 | 33.5 | 77.4 77.3 | 77.4 | 5.0 4.9 | 5.0 | 5.0 | 3.4 3.8 | 3.6 | 4.6 4.6 | | 4.6 | | |
| C2 | Sunny | Moderate | 10:55 | Surface | 1 | 29.7 29.7 | 29.7 | 8.2 8.2 | 8.2 | 31.0 31.0 | 31.0 | 77.8 78.0 | 77.9 | 5.0 5.0 | 5.0 | 5.0 | 5.0 | 1.2 1.3 | 1.3 | 2.9 | 5.5 5.5 | 5.5 | 5.9 |
| | | | | Middle | 17 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 32.4 32.4 | 32.4 | 77.2 77.2 | 77.2 | 4.9 4.9 | 4.9 | 4.9 | 3.7 3.5 | 3.6 | 7.0 6.8 | | 6.9 | | |
| | | | | Bottom | 33 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 33.4 33.5 | 33.5 | 77.2 77.9 | 77.6 | 4.9 5.0 | 5.0 | 5.0 | 4.3 3.5 | 3.9 | 5.4 5.3 | | 5.4 | | |
| G1 | Sunny | Moderate | 11:33 | Surface | 1 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 82.5 82.5 | 82.5 | 5.3 5.3 | 5.3 | 5.3 | 5.3 | 1.0 1.0 | 1.0 | 1.0 | 4.8 4.9 | 4.9 | 5.8 |
| | | | | Middle | 4 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 81.6 82.1 | 81.9 | 5.2 5.3 | 5.3 | 5.3 | 1.0 0.9 | 1.0 | 6.7 6.9 | | 6.8 | | |
| | | | | Bottom | 7 | 29.7 29.8 | 29.8 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 81.5 82.8 | 82.2 | 5.2 5.3 | 5.3 | 5.3 | 1.0 1.0 | 1.0 | 5.6 5.5 | | 5.6 | | |
| G2 | Sunny | Moderate | 11:19 | Surface | 1 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 81.5 82.6 | 82.1 | 5.2 5.3 | 5.3 | 5.3 | 5.3 | 1.1 1.0 | 1.1 | 1.4 | 3.6 3.5 | 3.6 | 5.8 |
| | | | | Middle | 4.5 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 81.2 82.0 | 81.6 | 5.2 5.2 | 5.2 | 5.2 | 1.0 0.9 | 1.0 | 7.8 7.7 | | 7.8 | | |
| | | | | Bottom | 8 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.4 31.4 | 31.4 | 80.4 77.0 | 78.7 | 5.1 4.9 | 5.0 | 5.0 | 2.2 2.1 | 2.2 | 6.0 6.0 | | 6.0 | | |
| G3 | Sunny | Moderate | 11:39 | Surface | 1 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 82.9 83.1 | 83.0 | 5.3 5.3 | 5.3 | 5.3 | 5.3 | 0.9 0.9 | 0.9 | 1.0 | 4.9 5.0 | 5.0 | 4.1 |
| | | | | Middle | 4 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 82.2 82.4 | 82.3 | 5.3 5.3 | 5.3 | 5.3 | 1.0 0.9 | 1.0 | 4.6 4.8 | | 4.7 | | |
| | | | | Bottom | 7 | 29.8 29.7 | 29.8 | 8.3 8.3 | 8.3 | 31.3 31.4 | 31.4 | 82.6 81.9 | 82.3 | 5.3 5.2 | 5.3 | 5.3 | 0.9 1.0 | 1.0 | 2.6 2.6 | | 2.6 | | |
| G4 | Sunny | Moderate | 12:00 | Surface | 1 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.1 31.1 | 31.1 | 78.5 77.6 | 78.1 | 5.0 5.0 | 5.0 | 5.0 | 5.0 | 1.9 2.1 | 2.0 | 2.7 | 4.0 4.0 | 4.0 | 4.1 |
| | | | | Middle | 4.5 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.2 31.2 | 31.2 | 77.2 76.9 | 77.1 | 4.9 4.9 | 4.9 | 4.9 | 3.4 3.3 | 3.4 | 4.1 4.1 | | 4.1 | | |
| | | | | Bottom | 8 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.4 | 31.4 | 77.4 77.6 | 77.5 | 5.0 5.0 | 5.0 | 5.0 | 2.6 2.6 | 2.6 | 4.1 4.0 | | 4.1 | | |
| M1 | Sunny | Moderate | 11:25 | Surface | 1 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 82.1 82.3 | 82.2 | 5.3 5.3 | 5.3 | 5.3 | 5.3 | 0.9 0.8 | 0.9 | 0.9 | 6.1 5.8 | 6.0 | 5.0 |
| | | | | Middle | 3 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 81.4 81.7 | 81.6 | 5.2 5.2 | 5.2 | 5.2 | 0.9 0.9 | 0.9 | 4.3 4.4 | | 4.4 | | |
| | | | | Bottom | 5 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 81.3 81.3 | 81.3 | 5.2 5.2 | 5.2 | 5.2 | 0.9 1.0 | 1.0 | 4.7 4.6 | | 4.7 | | |
| M2 | Sunny | Moderate | 11:10 | Surface | 1 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 81.7 82.2 | 82.0 | 5.2 5.3 | 5.3 | 5.3 | 5.3 | 0.9 0.9 | 0.9 | 1.8 | 6.1 5.9 | 6.0 | 4.9 |
| | | | | Middle | 6 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 81.6 81.5 | 81.6 | 5.2 5.2 | 5.2 | 5.2 | 0.8 0.9 | 0.9 | 4.7 4.6 | | 4.7 | | |
| | | | | Bottom | 11 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.4 31.5 | 31.5 | 78.1 75.1 | 75.6 | 4.9 4.8 | 4.9 | 4.9 | 3.7 3.6 | 3.7 | 4.0 4.1 | | 4.1 | | |
| M3 | Sunny | Moderate | 11:47 | Surface | 1 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 82.5 82.8 | 82.7 | 5.3 5.3 | 5.3 | 5.3 | 5.3 | 1.0 0.9 | 1.0 | 1.0 | 5.4 5.6 | 5.5 | 7.1 |
| | | | | Middle | 4 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 82.2 82.4 | 82.3 | 5.3 5.3 | 5.3 | 5.3 | 1.0 0.9 | 1.0 | 10.4 10.3 | | 10.4 | | |
| | | | | Bottom | 7 | 29.8 29.8 | 29.8 | 8.3 8.3 | 8.3 | 31.3 31.3 | 31.3 | 82.6 82.8 | 82.7 | 5.3 5.3 | 5.3 | 5.3 | 1.0 0.9 | 1.0 | 5.3 5.4 | | 5.4 | | |
| M4 | Sunny | Moderate | 11:03 | Surface | 1 | 29.7 29.7 | 29.7 | 8.2 8.3 | 8.3 | 31.3 31.3 | 31.3 | 83.2 82.1 | 82.7 | 5.3 5.3 | 5.3 | 5.3 | 5.3 | 1.0 0.9 | 1.0 | 1.4 | 5.6 5.3 | 5.5 | 4.5 |
| | | | | Middle | 5 | 29.7 29.7 | 29.7 | 8.2 8.3 | 8.3 | 31.3 31.3 | 31.3 | 81.8 81.3 | 81.6 | 5.2 5.2 | 5.2 | 5.2 | 1.0 1.0 | 1.0 | 4.4 4.3 | | 4.4 | | |
| | | | | Bottom | 9 | 29.7 29.7 | 29.7 | 8.2 8.3 | 8.3 | 31.4 31.4 | 31.4 | 76.7 76.9 | 76.8 | 4.9 4.9 | 4.9 | 4.9 | 2.3 2.2 | 2.3 | 3.5 3.5 | | 3.5 | | |
| M5 | Sunny | Moderate | 12:15 | Surface | 1 | 29.7 29.7 | 29.7 | 8.2 8.2 | 8.2 | 31.0 30.9 | 31.0 | 77.7 78.3 | 78.0 | 5.0 5.0 | 5.0 | 5.0 | 5.0 | 1.2 1.2 | 1.2 | 2.2 | 3.4 3.5 | 3.5 | 5.2 |
| | | | | Middle | 6 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.2 31.3 | 31.3 | 77.4 77.1 | 77.3 | 5.0 4.9 | 5.0 | 5.0 | 2.0 2.0 | 2.0 | 7.6 7.7 | | 7.7 | | |
| | | | | Bottom | 11 | 29.6 29.7 | 29.7 | 8.3 8.3 | 8.3 | 31.5 31.4 | 31.5 | 77.9 77.3 | 77.6 | 5.0 5.0 | 5.0 | 5.0 | 3.6 3.0 | 3.3 | 4.2 4.4 | | 4.3 | | |
| M6 | Sunny | Moderate | 12:08 | Surface | - | - | - | - | - | - | - | - | - | - | - | - | - | - | 1.2 | - | - | 7.6 | |
| | | | | Middle | 2.2 | 29.7 29.7 | 29.7 | 8.2 8.2 | 8.2 | 31.1 31.1 | 31.1 | 77.1 77.2 | 77.2 | 5.3 5.4 | 5.4 | 5.4 | 1.3 1.1 | 1.2 | | 7.4 7.7 | 7.6 | | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | - | - | - | | - | - | | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 4 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 4.7 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 5.1 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.5 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.0 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 04 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 18:45 | Surface | 1 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.4 31.4 | 31.4 | 73.6 72.2 | 72.9 | 5.4 5.3 | 5.4 | 5.3 | 1.5 1.4 | 1.5 | 3.0 | 4.8 4.9 | 4.9 | 4.7 |
| | | | | Middle | 9.5 | 27.0 27.0 | 27.0 | 8.3 8.3 | 8.3 | 32.8 33.0 | 32.9 | 69.4 67.9 | 68.7 | 5.1 5.0 | 5.1 | | 2.8 2.5 | 2.7 | | 4.3 4.3 | 4.3 | |
| | | | | Bottom | 18 | 26.9 26.9 | 26.9 | 8.3 8.3 | 8.3 | 33.4 33.5 | 33.5 | 64.8 64.5 | 64.7 | 4.8 4.7 | 4.8 | | 4.5 4.9 | 4.7 | | 4.9 4.9 | 4.9 | |
| C2 | Sunny | Moderate | 17:21 | Surface | 1 | 27.4 27.4 | 27.4 | 8.2 8.2 | 8.2 | 31.9 32.0 | 32.0 | 70.1 71.8 | 71.0 | 5.1 5.3 | 5.2 | 5.2 | 1.6 1.5 | 1.6 | 2.6 | 2.6 2.6 | 2.6 | 3.0 |
| | | | | Middle | 16.5 | 27.2 27.2 | 27.2 | 8.2 8.2 | 8.2 | 33.0 33.0 | 33.0 | 69.2 69.2 | 69.2 | 5.1 5.1 | 5.1 | | 2.9 2.4 | 2.7 | | 2.7 3.7 | 2.7 | |
| | | | | Bottom | 32 | 27.2 27.2 | 27.2 | 8.2 8.2 | 8.2 | 33.1 33.1 | 33.1 | 68.7 68.8 | 68.8 | 5.0 5.0 | 5.0 | | 3.5 3.3 | 3.4 | | 3.8 3.8 | 3.8 | |
| G1 | Sunny | Moderate | 18:00 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 31.2 31.2 | 31.2 | 78.2 77.5 | 77.9 | 5.3 5.2 | 5.3 | 5.2 | 0.9 0.9 | 0.9 | 1.3 | 2.8 2.8 | 2.8 | 3.7 |
| | | | | Middle | 4 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.4 31.4 | 31.4 | 75.3 75.1 | 75.2 | 5.1 5.1 | 5.1 | | 1.2 1.3 | 1.3 | | 4.2 4.2 | 4.2 | |
| | | | | Bottom | 7 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.5 31.4 | 31.5 | 74.6 74.7 | 74.7 | 5.0 5.0 | 5.0 | | 1.6 1.5 | 1.6 | | 4.1 4.2 | 4.2 | |
| G2 | Sunny | Moderate | 17:46 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 31.0 31.1 | 31.1 | 80.6 80.0 | 80.3 | 5.4 5.4 | 5.4 | 5.3 | 1.0 1.0 | 1.0 | 1.3 | 3.1 3.1 | 3.1 | 3.4 |
| | | | | Middle | 4.5 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.5 31.5 | 31.5 | 75.1 74.7 | 74.9 | 5.1 5.0 | 5.1 | | 1.3 1.2 | 1.3 | | 3.4 3.3 | 3.4 | |
| | | | | Bottom | 8 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.6 31.6 | 31.6 | 74.9 74.6 | 74.8 | 5.0 5.0 | 5.0 | | 1.5 1.4 | 1.5 | | 3.6 3.5 | 3.6 | |
| G3 | Sunny | Moderate | 18:07 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 31.0 30.9 | 31.0 | 79.4 78.8 | 79.1 | 5.4 5.3 | 5.4 | 5.3 | 0.9 1.1 | 1.0 | 1.2 | 3.9 3.8 | 3.9 | 4.2 |
| | | | | Middle | 4 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.4 31.4 | 31.4 | 76.7 76.3 | 76.5 | 5.2 5.1 | 5.2 | | 1.0 1.1 | 1.1 | | 4.8 4.9 | 4.9 | |
| | | | | Bottom | 7 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.7 31.6 | 31.7 | 76.8 76.8 | 76.8 | 5.2 5.2 | 5.2 | | 1.3 1.4 | 1.4 | | 3.7 3.7 | 3.7 | |
| G4 | Sunny | Moderate | 18:21 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 31.2 30.8 | 31.0 | 77.4 77.9 | 77.7 | 5.2 5.3 | 5.3 | 5.2 | 1.0 1.0 | 1.0 | 1.4 | 5.2 5.1 | 5.2 | 4.6 |
| | | | | Middle | 4.5 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.3 31.4 | 31.4 | 74.6 74.7 | 74.7 | 5.0 5.0 | 5.0 | | 1.3 1.4 | 1.4 | | 5.0 5.1 | 5.1 | |
| | | | | Bottom | 8 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.6 31.8 | 31.7 | 77.7 76.9 | 77.3 | 5.2 5.2 | 5.2 | | 1.6 1.7 | 1.7 | | 3.5 3.5 | 3.5 | |
| M1 | Sunny | Moderate | 17:53 | Surface | 1 | 27.5 27.5 | 27.5 | 8.3 8.3 | 8.3 | 31.2 31.1 | 31.2 | 88.3 89.0 | 88.7 | 6.0 6.0 | 6.0 | 5.8 | 1.1 0.9 | 1.0 | 1.3 | 4.3 4.5 | 4.4 | 4.9 |
| | | | | Middle | 3 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 31.3 31.4 | 31.4 | 81.0 84.3 | 82.7 | 5.5 5.7 | 5.6 | | 1.3 1.1 | 1.2 | | 4.8 4.9 | 4.9 | |
| | | | | Bottom | 5 | 27.3 27.4 | 27.4 | 8.3 8.3 | 8.3 | 31.5 31.5 | 31.5 | 80.1 80.3 | 80.2 | 5.4 5.4 | 5.4 | | 1.6 1.5 | 1.6 | | 5.1 5.4 | 5.3 | |
| M2 | Sunny | Moderate | 17:39 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 31.1 31.2 | 31.2 | 80.2 78.6 | 79.4 | 5.4 5.3 | 5.4 | 5.2 | 0.9 0.9 | 0.9 | 1.3 | 5.2 5.1 | 5.2 | 4.2 |
| | | | | Middle | 5.5 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.7 31.7 | 31.7 | 74.8 74.7 | 74.8 | 5.0 5.0 | 5.0 | | 1.4 1.3 | 1.4 | | 4.4 4.5 | 4.5 | |
| | | | | Bottom | 10 | 27.1 27.1 | 27.1 | 8.3 8.3 | 8.3 | 32.2 32.4 | 32.3 | 67.7 66.8 | 67.3 | 4.6 4.5 | 4.6 | | 1.6 1.7 | 1.7 | | 3.0 3.0 | 3.0 | |
| M3 | Sunny | Moderate | 18:13 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 30.8 30.6 | 30.7 | 79.7 78.9 | 79.3 | 5.4 5.3 | 5.4 | 5.4 | 0.9 1.0 | 1.0 | 1.2 | 2.7 2.6 | 2.7 | 3.0 |
| | | | | Middle | 4 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.4 31.5 | 31.5 | 78.3 77.7 | 78.0 | 5.3 5.2 | 5.3 | | 1.1 1.0 | 1.1 | | 3.3 3.3 | 3.3 | |
| | | | | Bottom | 7 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 31.6 31.6 | 31.6 | 77.4 77.2 | 77.3 | 5.2 5.2 | 5.2 | | 1.4 1.3 | 1.4 | | 3.1 3.1 | 3.1 | |
| M4 | Sunny | Moderate | 17:30 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 30.6 30.7 | 30.7 | 87.7 87.0 | 87.4 | 5.9 5.9 | 5.9 | 5.6 | 0.8 0.8 | 0.8 | 1.4 | 2.9 2.9 | 2.9 | 4.5 |
| | | | | Middle | 4.5 | 27.3 27.2 | 27.3 | 8.3 8.3 | 8.3 | 31.7 31.8 | 31.8 | 77.1 75.3 | 76.2 | 5.2 5.1 | 5.2 | | 1.6 1.4 | 1.5 | | 7.8 7.8 | 7.8 | |
| | | | | Bottom | 8 | 27.2 27.2 | 27.2 | 8.3 8.3 | 8.3 | 31.9 31.9 | 31.9 | 74.4 74.1 | 74.3 | 5.0 5.0 | 5.0 | | 1.9 1.6 | 1.8 | | 2.8 2.8 | 2.8 | |
| M5 | Sunny | Moderate | 18:36 | Surface | 1 | 27.4 27.4 | 27.4 | 8.2 8.3 | 8.3 | 31.0 31.0 | 31.0 | 73.4 72.5 | 73.0 | 5.2 5.1 | 5.2 | 5.2 | 1.0 1.0 | 1.0 | 1.7 | 3.0 3.0 | 3.0 | 2.9 |
| | | | | Middle | 6 | 27.4 27.3 | 27.4 | 8.3 8.3 | 8.3 | 31.2 31.3 | 31.3 | 72.6 72.0 | 72.3 | 5.1 5.1 | 5.1 | | 1.4 1.6 | 1.5 | | 2.6 2.7 | 2.7 | |
| | | | | Bottom | 11 | 27.0 27.0 | 27.0 | 8.3 8.3 | 8.3 | 32.7 32.7 | 32.7 | 65.5 64.5 | 65.0 | 4.4 4.3 | 4.4 | | 2.7 2.4 | 2.6 | | 2.9 2.9 | 2.9 | |
| M6 | Sunny | Moderate | 18:29 | Surface | - | - | - | - | - | - | - | - | - | - | 5.1 | - | - | 1.1 | - | - | 4.3 | |
| | | | | Middle | 2.2 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 31.1 31.1 | 31.1 | 76.0 75.6 | 75.8 | 5.1 5.1 | | 5.1 | 1.2 1.0 | | 1.1 | 4.2 4.3 | | 4.3 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 4 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 5.6 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 6.1 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 06 October 2017**

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|----------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|------------|-----|-----|------------|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | | | |
| C1 | Sunny | Calm | 13:05 | Surface | 1 | 27.4 27.4 | 27.4 | 8.6 8.6 | 8.6 | 27.6 27.4 | 27.5 | 82.9 83.3 | 83.1 | 5.6 5.7 | 5.7 | 5.3 | 1.4 1.4 | 1.4 | 2.6 | 4.9 5.0 | 5.0 | 4.9 | | |
| | | | | Middle | 10 | 24.3 24.4 | 24.4 | 8.6 8.6 | 8.6 | 33.7 33.6 | 33.7 | 71.2 71.3 | 71.3 | 4.9 4.9 | 4.9 | | | | | 3.0 3.1 | 3.1 | | 5.4 5.7 | 5.6 |
| | | | | Bottom | 19 | 23.8 23.7 | 23.8 | 8.6 8.6 | 8.6 | 34.3 34.4 | 34.4 | 66.6 69.6 | 68.1 | 4.6 4.8 | 4.7 | | | | | 3.0 3.5 | 3.3 | | 4.2 4.2 | 4.2 |
| C2 | Sunny | Calm | 11:02 | Surface | 1 | 27.5 27.6 | 27.6 | 8.5 8.6 | 8.6 | 27.0 27.2 | 27.1 | 86.7 84.8 | 85.8 | 5.9 5.8 | 5.9 | 5.1 | 1.1 1.1 | 1.1 | 3.7 | 5.7 5.8 | 5.8 | 4.7 | | |
| | | | | Middle | 17.5 | 24.0 23.9 | 24.0 | 8.5 8.6 | 8.6 | 34.1 34.2 | 34.2 | 61.7 62.6 | 62.2 | 4.3 4.3 | 4.3 | | | | | 4.0 4.3 | 4.2 | | 3.9 3.8 | 3.9 |
| | | | | Bottom | 34 | 23.9 23.8 | 23.9 | 8.6 8.6 | 8.6 | 34.2 34.3 | 34.3 | 62.5 65.4 | 64.0 | 4.3 4.5 | 4.4 | | | | | 5.9 5.7 | 5.8 | | 4.4 4.5 | 4.5 |
| G1 | Sunny | Calm | 12:05 | Surface | 1 | 27.5 27.6 | 27.6 | 8.8 8.7 | 8.8 | 27.7 28.5 | 28.1 | 96.8 97.5 | 97.2 | 6.6 6.6 | 6.6 | 6.0 | 1.0 1.0 | 1.0 | 1.3 | 5.4 5.6 | 5.5 | 4.8 | | |
| | | | | Middle | 4 | 26.4 26.2 | 26.3 | 8.6 8.6 | 8.6 | 30.6 30.9 | 30.8 | 81.0 78.4 | 79.7 | 5.5 5.3 | 5.4 | | | | | 0.9 1.0 | 1.0 | | 6.2 6.2 | 6.2 |
| | | | | Bottom | 7 | 24.4 24.4 | 24.4 | 8.5 8.5 | 8.5 | 34.0 34.0 | 34.0 | 73.3 70.0 | 71.7 | 5.1 4.8 | 5.0 | | | | | 1.9 1.8 | 1.9 | | 2.9 2.7 | 2.8 |
| G2 | Sunny | Calm | 11:42 | Surface | 1 | 27.4 28.3 | 27.9 | 8.7 8.7 | 8.7 | 28.4 28.9 | 28.7 | 117.4 116.9 | 117.2 | 7.9 7.8 | 7.9 | 6.7 | 1.1 1.0 | 1.1 | 1.4 | 4.6 4.7 | 4.7 | 4.3 | | |
| | | | | Middle | 4.5 | 26.1 28.3 | 27.2 | 8.6 8.6 | 8.6 | 31.1 31.9 | 31.5 | 76.7 87.2 | 82.0 | 5.2 5.7 | 5.5 | | | | | 1.0 1.0 | 1.0 | | 3.6 3.6 | 3.6 |
| | | | | Bottom | 8 | 24.4 27.9 | 26.2 | 8.5 8.5 | 8.5 | 34.0 32.6 | 33.3 | 74.9 80.0 | 77.5 | 5.2 5.2 | 5.2 | | | | | 2.1 2.1 | 2.1 | | 4.3 4.6 | 4.5 |
| G3 | Sunny | Calm | 12:16 | Surface | 1 | 27.4 27.4 | 27.4 | 8.7 8.7 | 8.7 | 28.4 28.5 | 28.5 | 105.3 103.4 | 104.4 | 7.1 7.0 | 7.1 | 6.0 | 1.2 1.1 | 1.2 | 1.4 | 4.1 4.2 | 4.2 | 4.1 | | |
| | | | | Middle | 4 | 26.4 26.3 | 26.4 | 8.6 8.6 | 8.6 | 30.7 30.9 | 30.8 | 74.5 69.6 | 72.1 | 5.1 4.7 | 4.9 | | | | | 1.0 0.9 | 1.0 | | 4.7 4.6 | 4.7 |
| | | | | Bottom | 7 | 24.8 24.7 | 24.8 | 8.5 8.5 | 8.5 | 33.4 33.6 | 33.5 | 68.0 63.4 | 65.7 | 4.7 4.4 | 4.6 | | | | | 1.9 1.8 | 1.9 | | 3.4 3.3 | 3.4 |
| G4 | Sunny | Calm | 12:42 | Surface | 1 | 27.5 27.3 | 27.4 | 8.7 8.7 | 8.7 | 28.7 29.0 | 28.9 | 116.2 101.7 | 109.0 | 7.8 6.9 | 7.4 | 6.3 | 4.8 4.7 | 4.8 | 2.8 | 3.7 3.6 | 3.7 | 3.7 | | |
| | | | | Middle | 4.5 | 26.6 25.9 | 26.3 | 8.6 8.6 | 8.6 | 30.3 31.4 | 30.9 | 80.1 70.1 | 75.1 | 5.4 4.8 | 5.1 | | | | | 0.8 0.9 | 0.9 | | 3.5 3.4 | 3.5 |
| | | | | Bottom | 8 | 24.5 24.5 | 24.5 | 8.5 8.5 | 8.5 | 33.9 33.9 | 33.9 | 63.4 63.6 | 63.5 | 4.4 4.4 | 4.4 | | | | | 2.7 2.7 | 2.7 | | 3.8 4.0 | 3.9 |
| M1 | Sunny | Calm | 11:54 | Surface | 1 | 27.5 27.5 | 27.5 | 8.7 8.7 | 8.7 | 28.5 28.4 | 28.5 | 118.3 118.6 | 118.5 | 8.0 8.0 | 8.0 | 7.2 | 1.1 1.0 | 1.1 | 1.5 | 3.7 3.7 | 3.7 | 4.0 | | |
| | | | | Middle | 3 | 27.0 27.1 | 27.1 | 8.6 8.6 | 8.6 | 29.3 29.2 | 29.3 | 93.1 96.0 | 94.6 | 6.3 6.5 | 6.4 | | | | | 1.4 1.4 | 1.4 | | 4.0 4.1 | 4.1 |
| | | | | Bottom | 5 | 26.0 25.9 | 26.0 | 8.6 8.6 | 8.6 | 31.3 31.5 | 31.4 | 92.6 89.7 | 91.2 | 6.3 6.1 | 6.2 | | | | | 2.1 2.1 | 2.1 | | 4.2 4.2 | 4.2 |
| M2 | Sunny | Calm | 11:31 | Surface | 1 | 27.5 27.4 | 27.5 | 8.8 8.7 | 8.8 | 28.2 28.2 | 28.2 | 121.6 118.5 | 120.1 | 8.2 8.0 | 8.1 | 6.1 | 1.3 1.3 | 1.3 | 2.9 | 3.5 3.5 | 3.5 | 3.9 | | |
| | | | | Middle | 6 | 25.4 25.2 | 25.3 | 8.5 8.5 | 8.5 | 32.5 32.7 | 32.6 | 59.0 56.7 | 57.9 | 4.0 3.9 | 4.0 | | | | | 1.1 1.1 | 1.1 | | 3.4 3.3 | 3.4 |
| | | | | Bottom | 11 | 24.1 24.0 | 24.1 | 8.5 8.6 | 8.6 | 34.2 34.2 | 34.2 | 78.8 78.4 | 78.6 | 5.5 5.4 | 5.5 | | | | | 6.2 6.3 | 6.3 | | 4.9 4.9 | 4.9 |
| M3 | Sunny | Calm | 12:28 | Surface | 1 | 26.7 26.4 | 26.6 | 8.6 8.6 | 8.6 | 29.8 30.1 | 30.0 | 81.0 80.6 | 80.8 | 5.5 5.5 | 5.5 | 5.3 | 2.0 2.4 | 2.2 | 3.7 | 3.7 3.6 | 3.7 | 4.7 | | |
| | | | | Middle | 4 | 26.1 26.0 | 26.1 | 8.6 8.5 | 8.6 | 31.2 31.3 | 31.3 | 73.1 72.4 | 72.8 | 5.0 4.9 | 5.0 | | | | | 3.9 4.1 | 4.0 | | 6.1 6.3 | 6.2 |
| | | | | Bottom | 7 | 25.0 25.1 | 25.1 | 8.5 8.5 | 8.5 | 33.1 33.0 | 33.1 | 66.3 69.3 | 67.8 | 4.5 4.7 | 4.6 | | | | | 4.9 5.1 | 5.0 | | 4.3 4.2 | 4.3 |
| M4 | Sunny | Calm | 11:23 | Surface | 1 | 27.4 27.4 | 27.4 | 8.7 8.7 | 8.7 | 28.5 28.5 | 28.5 | 113.9 111.9 | 112.9 | 7.7 7.6 | 7.7 | 6.6 | 1.2 1.0 | 1.1 | 1.2 | 4.1 4.1 | 4.1 | 3.8 | | |
| | | | | Middle | 5.5 | 26.6 26.3 | 26.5 | 8.6 8.6 | 8.6 | 30.3 30.9 | 30.6 | 84.3 78.7 | 81.5 | 5.7 5.3 | 5.5 | | | | | 0.8 0.8 | 0.8 | | 3.5 3.5 | 3.5 |
| | | | | Bottom | 10 | 24.5 24.6 | 24.6 | 8.5 8.6 | 8.6 | 33.5 33.5 | 33.5 | 80.9 80.8 | 80.9 | 5.6 5.6 | 5.6 | | | | | 1.8 1.7 | 1.8 | | 3.9 3.9 | 3.9 |
| M5 | Sunny | Calm | 12:56 | Surface | 1 | 27.3 27.1 | 27.2 | 8.7 8.7 | 8.7 | 28.0 28.6 | 28.3 | 105.7 97.6 | 101.7 | 7.2 6.6 | 6.9 | 5.6 | 1.1 1.2 | 1.2 | 2.2 | 4.9 5.0 | 5.0 | 4.6 | | |
| | | | | Middle | 6 | 25.0 25.2 | 25.1 | 8.5 8.6 | 8.6 | 32.9 32.5 | 32.7 | 59.1 61.5 | 60.3 | 4.1 4.2 | 4.2 | | | | | 1.5 1.6 | 1.6 | | 4.4 4.5 | 4.5 |
| | | | | Bottom | 11 | 24.1 24.1 | 24.1 | 8.6 8.6 | 8.6 | 34.2 34.2 | 34.2 | 79.4 78.5 | 79.0 | 5.5 5.4 | 5.5 | | | | | 3.7 3.6 | 3.7 | | 4.4 4.4 | 4.4 |
| M6 | Sunny | Calm | 12:49 | Surface | - | - | - | - | - | - | - | - | - | - | - | 7.8 | - | - | 4.4 | - | - | 5.6 | | |
| | | | | Middle | 1.4 | 27.5 27.5 | 27.5 | 8.7 8.7 | 8.7 | 28.6 28.5 | 28.6 | 114.9 116.6 | 115.8 | 7.7 7.9 | 7.8 | | | | | 4.5 4.2 | 4.4 | | 5.6 5.6 | 5.6 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | | | | | - | - | | - | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 6 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|--|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 7.0 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 7.5 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.0 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.5 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.0 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.5 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.4 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 5.9 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 06 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|----------------|-------------------------|-------------|------|----------------|------------|-----|-------------------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Fine | Calm | 19:03 | Surface | 1 | 27.9 27.9 | 27.9 | 8.9 8.9 | 8.9 | 28.8 28.8 | 28.8 | 140.3 139.6 | 140.0 | 9.4 9.3 | 9.4 | 7.0 | 0.9 0.8 | 0.9 | 3.7 | 4.1 4.2 | 4.2 | 4.2 |
| | | | | Middle | 9.5 | 24.1 24.2 | 24.2 | 8.6 8.6 | 8.6 | 33.9 33.9 | 33.9 | 66.4 66.4 | 66.4 | 4.6 4.6 | 4.6 | 4.6 | 2.3 2.2 | 2.3 | | 3.5 3.5 | 3.5 | |
| | | | | Bottom | 18 | 23.6 23.6 | 23.6 | 8.6 8.6 | 8.6 | 34.4 34.4 | 34.4 | 73.4 73.1 | 73.3 | 5.1 5.1 | 5.1 | 5.1 | 8.1 7.5 | 7.8 | | 4.8 4.9 | 4.9 | |
| C2 | Fine | Calm | 17:22 | Surface | 1 | 27.9 27.9 | 27.9 | 8.8 8.9 | 8.9 | 28.3 28.1 | 28.2 | 148.4 148.5 | 148.5 | 9.9 10.0 | 10.0 | 7.2 | 1.9 2.0 | 2.0 | 3.2 | 3.1 3.0 | 3.1 | 2.9 |
| | | | | Middle | 16.5 | 24.3 24.3 | 24.3 | 8.5 8.6 | 8.6 | 33.8 33.8 | 33.8 | 61.5 61.7 | 61.6 | 4.3 4.3 | 4.3 | 4.3 | 2.3 2.3 | 2.3 | | 3.0 3.1 | 3.1 | |
| | | | | Bottom | 32 | 23.9 23.9 | 23.9 | 8.6 8.6 | 8.6 | 34.2 34.2 | 34.2 | 66.6 66.5 | 66.6 | 4.6 4.6 | 4.6 | 4.6 | 5.8 5.0 | 5.4 | | 2.6 2.6 | 2.6 | |
| G1 | Fine | Calm | 18:15 | Surface | 1 | 27.3 27.6 | 27.5 | 8.8 7.9 | 8.4 | 28.3 25.5 | 26.9 | 123.9 112.0 | 118.0 | 8.4 7.7 | 8.1 | 7.2 | 1.6 1.8 | 1.7 | 1.5 | 4.5 4.2 | 4.4 | 5.3 |
| | | | | Middle | 3.5 | 26.7 26.7 | 26.7 | 8.7 8.7 | 8.7 | 29.7 29.7 | 29.7 | 92.1 91.8 | 92.0 | 6.3 6.2 | 6.3 | 6.3 | 1.3 1.4 | 1.4 | | 7.2 7.6 | 7.4 | |
| | | | | Bottom | 6 | 25.3 25.3 | 25.3 | 8.6 8.6 | 8.6 | 32.2 32.2 | 32.2 | 65.8 66.1 | 66.0 | 4.5 4.5 | 4.5 | 4.5 | 1.4 1.4 | 1.4 | | 4.0 3.9 | 4.0 | |
| G2 | Fine | Calm | 17:58 | Surface | 1 | 27.4 27.2 | 27.3 | 8.8 8.8 | 8.8 | 28.0 28.2 | 28.1 | 97.1 97.3 | 97.2 | 6.6 6.6 | 6.6 | 6.1 | 1.9 1.8 | 1.9 | 1.5 | 4.6 4.6 | 4.6 | 4.6 |
| | | | | Middle | 4 | 26.3 26.1 | 26.2 | 8.6 8.6 | 8.6 | 30.4 30.7 | 30.6 | 82.3 79.0 | 80.7 | 5.6 5.4 | 5.5 | 5.5 | 1.3 1.3 | 1.3 | | 4.9 4.7 | 4.8 | |
| | | | | Bottom | 7 | 24.9 25.0 | 25.0 | 8.5 8.6 | 8.6 | 33.2 33.0 | 33.1 | 75.5 79.5 | 77.5 | 5.2 5.5 | 5.4 | 5.4 | 1.3 1.3 | 1.3 | | 4.3 4.4 | 4.4 | |
| G3 | Fine | Calm | 18:25 | Surface | 1 | 27.5 27.5 | 27.5 | 8.8 8.8 | 8.8 | 28.0 27.8 | 27.9 | 94.9 96.0 | 95.5 | 6.4 6.5 | 6.5 | 6.2 | 1.9 1.8 | 1.9 | 1.6 | 3.6 3.6 | 3.6 | 3.9 |
| | | | | Middle | 3.5 | 27.1 27.2 | 27.2 | 8.7 8.7 | 8.7 | 29.2 29.1 | 29.2 | 85.1 84.3 | 84.7 | 5.8 5.7 | 5.8 | 5.8 | 1.2 1.1 | 1.2 | | 4.5 4.5 | 4.5 | |
| | | | | Bottom | 6 | 25.2 25.3 | 25.3 | 8.5 8.5 | 8.5 | 32.8 32.7 | 32.8 | 70.2 73.4 | 71.8 | 4.8 5.0 | 4.9 | 4.9 | 1.8 1.5 | 1.7 | | 3.7 3.6 | 3.7 | |
| G4 | Fine | Calm | 18:40 | Surface | 1 | 27.5 27.4 | 27.5 | 8.8 8.8 | 8.8 | 27.9 27.9 | 27.9 | 100.1 98.9 | 99.5 | 6.8 6.7 | 6.8 | 6.3 | 1.9 1.9 | 1.9 | 1.5 | 3.5 3.7 | 3.6 | 4.1 |
| | | | | Middle | 4 | 27.0 27.0 | 27.0 | 8.7 8.7 | 8.7 | 29.3 29.3 | 29.3 | 83.0 84.1 | 83.6 | 5.6 5.7 | 5.7 | 5.7 | 1.1 1.3 | 1.2 | | 4.4 4.4 | 4.4 | |
| | | | | Bottom | 7 | 25.1 25.0 | 25.1 | 8.5 8.5 | 8.5 | 32.9 33.0 | 33.0 | 73.2 76.7 | 75.0 | 5.0 5.3 | 5.2 | 5.2 | 1.4 1.3 | 1.4 | | 4.3 4.1 | 4.2 | |
| M1 | Fine | Calm | 18:07 | Surface | 1 | 27.1 27.1 | 27.1 | 8.7 8.7 | 8.7 | 28.7 28.6 | 28.7 | 95.6 96.7 | 96.2 | 6.5 6.6 | 6.6 | 6.3 | 1.5 1.7 | 1.6 | 1.6 | 3.0 2.8 | 2.9 | 3.9 |
| | | | | Middle | 3 | 27.0 27.0 | 27.0 | 8.7 8.7 | 8.7 | 29.1 29.1 | 29.1 | 86.9 87.0 | 87.0 | 5.9 5.9 | 5.9 | 5.9 | 1.2 1.3 | 1.3 | | 3.5 3.4 | 3.5 | |
| | | | | Bottom | 5 | 25.5 25.4 | 25.5 | 8.5 8.6 | 8.6 | 32.3 32.4 | 32.4 | 82.8 81.3 | 82.1 | 5.7 5.6 | 5.7 | 5.7 | 1.7 1.9 | 1.8 | | 5.3 5.3 | 5.3 | |
| M2 | Fine | Calm | 17:49 | Surface | 1 | 27.2 27.4 | 27.3 | 8.7 8.8 | 8.8 | 28.4 28.0 | 28.2 | 111.1 112.9 | 112.0 | 7.5 7.6 | 7.6 | 6.4 | 1.5 1.7 | 1.6 | 1.4 | 3.5 3.5 | 3.5 | 3.7 |
| | | | | Middle | 5 | 26.3 26.1 | 26.2 | 8.6 8.6 | 8.6 | 30.7 31.2 | 31.0 | 79.4 72.7 | 76.1 | 5.4 4.9 | 5.2 | 5.3 | 1.1 1.3 | 1.2 | | 4.0 4.1 | 4.1 | |
| | | | | Bottom | 9 | 24.4 24.4 | 24.4 | 8.5 8.6 | 8.6 | 33.8 33.8 | 33.8 | 76.5 77.4 | 77.0 | 5.3 5.3 | 5.3 | 5.3 | 1.3 1.4 | 1.4 | | 3.7 3.5 | 3.6 | |
| M3 | Fine | Calm | 18:31 | Surface | 1 | 27.6 27.5 | 27.6 | 8.8 8.8 | 8.8 | 27.4 27.8 | 27.6 | 102.5 102.7 | 102.6 | 6.9 7.0 | 7.0 | 6.8 | 2.0 1.8 | 1.9 | 1.6 | 3.2 3.3 | 3.3 | 3.4 |
| | | | | Middle | 3.5 | 27.1 27.1 | 27.1 | 8.7 8.7 | 8.7 | 29.3 29.2 | 29.3 | 93.9 97.3 | 95.6 | 6.3 6.6 | 6.5 | 6.5 | 1.0 1.0 | 1.0 | | 3.6 3.5 | 3.6 | |
| | | | | Bottom | 6 | 25.3 25.4 | 25.4 | 8.5 8.5 | 8.5 | 32.6 32.6 | 32.6 | 72.1 72.8 | 72.5 | 4.9 5.0 | 5.0 | 5.0 | 1.9 1.8 | 1.9 | | 3.2 3.3 | 3.3 | |
| M4 | Fine | Calm | 17:39 | Surface | 1 | 27.5 27.6 | 27.6 | 8.8 8.8 | 8.8 | 28.4 28.1 | 28.3 | 102.0 101.2 | 101.6 | 6.9 6.8 | 6.9 | 6.6 | 1.3 1.2 | 1.3 | 1.1 | 4.3 4.4 | 4.4 | 3.5 |
| | | | | Middle | 4.5 | 26.8 26.9 | 26.9 | 8.6 8.7 | 8.7 | 29.9 29.7 | 29.8 | 90.2 93.7 | 92.0 | 6.1 6.3 | 6.2 | 6.2 | 1.0 0.9 | 1.0 | | 2.6 2.5 | 2.6 | |
| | | | | Bottom | 8 | 25.9 25.7 | 25.8 | 8.6 8.6 | 8.6 | 31.5 31.8 | 31.7 | 92.1 90.7 | 91.4 | 6.3 6.2 | 6.3 | 6.3 | 0.8 0.9 | 0.9 | | 3.3 3.4 | 3.4 | |
| M5 | Fine | Calm | 18:54 | Surface | 1 | 27.4 27.5 | 27.5 | 8.7 8.7 | 8.7 | 28.6 28.4 | 28.5 | 118.2 118.6 | 118.4 | 8.0 8.0 | 8.0 | 6.6 | 1.2 1.1 | 1.2 | 2.6 | 3.3 3.4 | 3.4 | 3.7 |
| | | | | Middle | 5.5 | 26.1 26.3 | 26.2 | 8.6 8.6 | 8.6 | 30.9 30.7 | 30.8 | 75.7 76.5 | 76.1 | 5.2 5.2 | 5.2 | 5.2 | 1.4 1.3 | 1.4 | | 4.2 4.3 | 4.3 | |
| | | | | Bottom | 10 | 24.2 24.2 | 24.2 | 8.6 8.6 | 8.6 | 33.9 33.9 | 33.9 | 80.1 77.1 | 78.6 | 5.5 5.3 | 5.4 | 5.4 | 5.3 5.3 | 5.3 | | 3.2 3.3 | 3.3 | |
| M6 | Fine | Calm | 18:47 | Surface | - | - | - | - | - | - | - | - | - | - | - | 7.9 | - | - | 1.7 | - | - | 4.9 |
| | | | | Middle | 2.2 | 27.2 27.3 | 27.3 | 8.7 8.7 | 8.7 | 28.5 28.4 | 28.5 | 115.1 116.3 | 115.7 | 7.8 7.9 | 7.9 | 7.9 | 1.7 1.6 | 1.7 | | 4.9 4.8 | 4.9 | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | - | - | - | | - | - | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 6 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|--|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 9.4 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 10.1 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.0 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.5 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.0 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.5 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 09 October 2017**

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|----------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 15:46 | Surface | 1 | 28.9 27.4 | 28.2 | 8.7 8.7 | 8.7 | 30.2 30.9 | 30.6 | 109.7 102.1 | 105.9 | 7.2 6.8 | 7.0 | 6.3 | 3.1 3.1 | 3.1 | 4.5 | 4.1 3.9 | 4.0 | 4.4 |
| | | | | Middle | 9.5 | 26.7 25.4 | 26.1 | 8.5 8.5 | 8.5 | 31.4 31.0 | 31.2 | 83.1 77.7 | 80.4 | 5.6 5.4 | 5.5 | | 3.7 3.7 | 3.7 | | 5.3 5.4 | 5.4 | |
| | | | | Bottom | 18 | 24.7 23.5 | 24.1 | 8.4 8.4 | 8.4 | 31.3 31.7 | 31.5 | 66.1 64.2 | 65.2 | 4.6 4.6 | 4.6 | | 6.5 6.6 | 6.6 | | 3.9 3.8 | 3.9 | |
| C2 | Sunny | Moderate | 14:09 | Surface | 1 | 28.7 28.8 | 28.8 | 8.5 8.7 | 8.6 | 29.9 29.7 | 29.8 | 112.0 111.4 | 111.7 | 7.3 7.3 | 7.3 | 6.3 | 3.3 3.3 | 3.3 | 4.7 | 4.1 4.2 | 4.2 | 4.4 |
| | | | | Middle | 17 | 26.4 26.4 | 26.4 | 8.4 8.5 | 8.5 | 31.8 31.8 | 31.8 | 78.2 77.4 | 76.8 | 5.1 5.2 | 5.2 | | 4.4 4.1 | 4.3 | | 2.7 2.7 | 2.7 | |
| | | | | Bottom | 33 | 26.0 26.1 | 26.1 | 8.4 8.4 | 8.4 | 32.9 32.7 | 32.8 | 68.1 67.4 | 67.8 | 4.6 4.5 | 4.6 | | 6.3 6.4 | 6.4 | | 6.5 6.3 | 6.4 | |
| G1 | Sunny | Moderate | 15:02 | Surface | 1 | 27.8 27.9 | 27.9 | 8.6 8.6 | 8.6 | 30.7 30.7 | 30.7 | 94.9 94.9 | 94.9 | 6.3 6.3 | 6.3 | 6.2 | 3.4 3.4 | 3.4 | 3.8 | 4.1 4.1 | 4.1 | 3.7 |
| | | | | Middle | 3 | 27.8 27.7 | 27.8 | 8.6 8.6 | 8.6 | 30.7 30.8 | 30.8 | 93.0 89.5 | 91.3 | 6.2 5.9 | 6.1 | | 3.5 3.8 | 3.7 | | 3.6 3.6 | 3.6 | |
| | | | | Bottom | 5 | 27.5 27.5 | 27.5 | 8.6 8.6 | 8.6 | 31.0 31.0 | 31.0 | 84.5 83.2 | 83.9 | 5.6 5.5 | 5.6 | | 4.4 4.1 | 4.3 | | 3.5 3.5 | 3.5 | |
| G2 | Sunny | Moderate | 14:40 | Surface | 1 | 28.0 28.0 | 28.0 | 8.7 8.7 | 8.7 | 30.2 30.2 | 30.2 | 98.9 99.5 | 99.2 | 6.6 6.6 | 6.6 | 6.2 | 3.9 3.7 | 3.8 | 4.2 | 2.8 2.8 | 2.8 | 3.4 |
| | | | | Middle | 4 | 27.6 27.6 | 27.6 | 8.6 8.6 | 8.6 | 30.8 30.9 | 30.9 | 87.9 87.7 | 87.8 | 5.8 5.8 | 5.8 | | 3.4 3.3 | 3.4 | | 3.2 3.2 | 3.2 | |
| | | | | Bottom | 7 | 27.2 27.3 | 27.3 | 8.6 8.6 | 8.6 | 31.3 31.2 | 31.3 | 74.6 80.6 | 77.6 | 5.0 5.4 | 5.2 | | 5.6 4.9 | 5.3 | | 4.2 4.1 | 4.2 | |
| G3 | Sunny | Moderate | 15:09 | Surface | 1 | 28.2 28.0 | 28.1 | 8.7 8.7 | 8.7 | 29.8 30.0 | 29.9 | 108.8 99.3 | 104.1 | 7.2 6.6 | 6.9 | 6.2 | 3.7 3.6 | 3.7 | 5.0 | 3.9 4.0 | 4.0 | 3.9 |
| | | | | Middle | 3.5 | 27.5 27.5 | 27.5 | 8.6 8.6 | 8.6 | 30.9 30.9 | 30.9 | 82.0 81.4 | 81.7 | 5.5 5.4 | 5.5 | | 4.1 4.0 | 4.1 | | 4.7 4.7 | 4.7 | |
| | | | | Bottom | 6 | 27.1 27.1 | 27.1 | 8.5 8.5 | 8.5 | 31.3 31.3 | 31.3 | 69.5 69.2 | 69.4 | 4.6 4.6 | 4.6 | | 7.3 7.1 | 7.2 | | 3.0 3.1 | 3.1 | |
| G4 | Sunny | Moderate | 15:25 | Surface | 1 | 28.0 27.9 | 28.0 | 8.7 8.7 | 8.7 | 30.6 30.6 | 30.6 | 99.4 99.3 | 99.4 | 6.6 6.6 | 6.6 | 6.4 | 4.2 4.4 | 4.3 | 4.1 | 4.8 4.5 | 4.7 | 3.6 |
| | | | | Middle | 4 | 27.8 27.8 | 27.8 | 8.6 8.6 | 8.6 | 30.8 30.8 | 30.8 | 92.6 93.4 | 93.0 | 6.1 6.2 | 6.2 | | 3.4 3.3 | 3.4 | | 3.5 3.5 | 3.5 | |
| | | | | Bottom | 7 | 27.5 27.5 | 27.5 | 8.6 8.6 | 8.6 | 30.9 31.0 | 31.0 | 83.1 83.2 | 83.2 | 5.5 5.5 | 5.5 | | 4.6 4.6 | 4.6 | | 2.7 2.7 | 2.7 | |
| M1 | Sunny | Moderate | 14:51 | Surface | 1 | 27.7 27.7 | 27.7 | 8.6 8.6 | 8.6 | 30.6 30.5 | 30.6 | 89.2 88.6 | 88.9 | 5.9 5.9 | 5.9 | 5.9 | 4.2 4.1 | 4.2 | 4.3 | 4.1 4.0 | 4.1 | 4.1 |
| | | | | Middle | 3 | 27.7 27.7 | 27.7 | 8.6 8.6 | 8.6 | 30.8 30.7 | 30.8 | 88.8 88.8 | 88.8 | 5.9 5.9 | 5.9 | | 3.8 3.8 | 3.8 | | 3.6 3.7 | 3.7 | |
| | | | | Bottom | 5 | 27.4 27.6 | 27.5 | 8.6 8.6 | 8.6 | 31.0 30.8 | 30.9 | 78.6 85.4 | 82.0 | 5.2 5.7 | 5.5 | | 4.7 4.8 | 4.8 | | 4.6 4.6 | 4.6 | |
| M2 | Sunny | Moderate | 14:29 | Surface | 1 | 28.2 28.4 | 28.3 | 8.7 8.7 | 8.7 | 30.1 30.0 | 30.1 | 110.1 113.6 | 111.9 | 7.3 7.5 | 7.4 | 6.5 | 3.5 3.4 | 3.5 | 4.6 | 3.3 3.5 | 3.4 | 3.7 |
| | | | | Middle | 5.5 | 27.6 27.5 | 27.6 | 8.6 8.6 | 8.6 | 30.9 31.0 | 31.0 | 84.2 83.5 | 83.9 | 5.6 5.6 | 5.6 | | 3.6 3.7 | 3.7 | | 4.0 3.8 | 3.9 | |
| | | | | Bottom | 10 | 28.3 27.1 | 27.7 | 8.7 8.5 | 8.6 | 29.7 31.5 | 30.6 | 71.4 72.4 | 71.9 | 4.7 4.8 | 4.8 | | 6.4 6.5 | 6.5 | | 3.7 3.9 | 3.8 | |
| M3 | Sunny | Moderate | 15:15 | Surface | 1 | 28.0 28.0 | 28.0 | 8.7 8.7 | 8.7 | 29.9 30.0 | 30.0 | 97.4 97.5 | 97.5 | 6.5 6.5 | 6.5 | 5.8 | 3.7 3.8 | 3.8 | 5.3 | 4.5 4.7 | 4.6 | 4.7 |
| | | | | Middle | 3.5 | 27.3 27.4 | 27.4 | 8.5 8.5 | 8.5 | 30.8 30.8 | 30.8 | 76.6 76.8 | 76.7 | 5.1 5.1 | 5.1 | | 5.6 5.2 | 5.4 | | 4.1 4.0 | 4.1 | |
| | | | | Bottom | 6 | 27.1 27.1 | 27.1 | 8.5 8.5 | 8.5 | 31.2 31.2 | 31.2 | 67.5 68.3 | 67.9 | 4.5 4.6 | 4.6 | | 7.1 6.5 | 6.8 | | 5.6 5.4 | 5.5 | |
| M4 | Sunny | Moderate | 14:19 | Surface | 1 | 28.9 28.9 | 28.9 | 8.8 8.8 | 8.8 | 29.5 29.5 | 29.5 | 120.3 119.8 | 120.1 | 7.9 7.8 | 7.9 | 7.4 | 3.5 3.4 | 3.5 | 3.5 | 4.0 4.0 | 4.0 | 3.9 |
| | | | | Middle | 4.5 | 28.0 28.0 | 28.0 | 8.7 8.7 | 8.7 | 30.2 30.2 | 30.2 | 102.7 104.1 | 103.4 | 6.8 6.9 | 6.9 | | 3.4 3.4 | 3.4 | | 3.5 3.6 | 3.6 | |
| | | | | Bottom | 8 | 28.0 27.9 | 28.0 | 8.6 8.7 | 8.7 | 30.5 30.3 | 30.4 | 90.0 96.7 | 93.4 | 6.0 6.4 | 6.2 | | 3.6 3.5 | 3.6 | | 4.0 4.1 | 4.1 | |
| M5 | Sunny | Moderate | 15:37 | Surface | 1 | 27.6 27.6 | 27.6 | 8.6 8.6 | 8.6 | 30.9 30.9 | 30.9 | 86.3 86.3 | 86.3 | 5.7 5.7 | 5.7 | 5.6 | 4.3 4.2 | 4.3 | 4.6 | 3.4 3.5 | 3.5 | 3.3 |
| | | | | Middle | 5.5 | 27.4 27.2 | 27.3 | 8.6 8.6 | 8.6 | 31.2 31.4 | 31.3 | 82.7 79.1 | 80.9 | 5.5 5.3 | 5.4 | | 4.4 4.2 | 4.3 | | 3.7 3.6 | 3.7 | |
| | | | | Bottom | 10 | 27.1 27.2 | 27.2 | 8.6 8.6 | 8.6 | 31.5 31.4 | 31.5 | 76.5 77.3 | 76.9 | 5.1 5.2 | 5.2 | | 5.3 5.3 | 5.3 | | 2.7 2.8 | 2.8 | |
| M6 | Sunny | Moderate | 15:32 | Surface | - | - | - | - | - | - | - | - | - | - | - | 6.4 | - | - | 3.7 | - | - | 3.6 |
| | | | | Middle | 2.1 | 27.8 27.8 | 27.8 | 8.6 8.6 | 8.6 | 30.7 30.6 | 30.7 | 95.9 96.2 | 96.1 | 6.4 6.4 | 6.4 | | 3.7 3.7 | 3.7 | | 3.6 3.6 | 3.6 | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 9 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 7.7 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 8.3 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.0 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 5.5mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.0 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 5.5 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.7 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 8.3 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 09 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | | | | | | | | | | | |
|----------|-------------------|-----------------|---------------|------------|------------------|--------------|-------|----------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|------------|-------------------------|------------|------------|-----|------------|------------|------------|------------|------------|-----|-----|------------|------------|------------|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | | | | | | | | | | | |
| C1 | Sunny | Moderate | 10:12 | Surface | 1 | 27.4 27.3 | 27.4 | 8.5 8.5 | 8.5 | 30.2 30.2 | 30.2 | 91.4 88.4 | 89.9 | 6.1 5.9 | 6.0 | 5.7 | 3.5 3.5 | 3.5 | 4.1 | 4.4 4.5 | 4.5 | 4.4 | | | | | | | | | | |
| | | | | Middle | 9.5 | 26.6 26.7 | 26.7 | 8.4 8.4 | 8.4 | 30.8 30.6 | 30.7 | 80.1 77.2 | 78.7 | 5.4 5.2 | 5.3 | | | | | | | | 3.8 3.7 | 3.8 | 5.0 5.1 | 5.0 5.1 | 3.5 3.5 | 3.5 | 4.4 | | | |
| | | | | Bottom | 18 | 25.4 23.8 | 24.6 | 8.3 8.2 | 8.3 | 31.9 31.7 | 31.8 | 66.4 63.4 | 64.9 | 4.6 4.5 | 4.6 | | | | | | | | | | | | | | | 4.6 | 5.2 5.2 | 5.1 |
| Surface | 1 | 26.7 26.7 | 26.7 | 8.4 8.4 | 8.4 | 29.9 29.9 | 29.9 | 82.8 83.1 | 83.0 | 5.6 5.6 | 5.6 | 5.4 | 3.6 3.5 | 3.6 | 4.5 | 4.2 | 4.5 | 4.4 | 4.6 | | | | | | | | | | | | | |
| Middle | 17 | 26.0 26.0 | 26.0 | 8.4 8.3 | 8.4 | 31.6 31.7 | 31.7 | 75.2 74.5 | 74.9 | 5.1 5.1 | 5.1 | | | | | | | | | 4.6 | 4.8 4.7 | 4.8 | 5.0 5.0 | 4.9 | 5.5 5.6 | 5.5 | 5.6 | 4.6 | | | | |
| Bottom | 33 | 25.8 25.7 | 25.8 | 8.3 8.3 | 8.3 | 32.1 32.2 | 32.2 | 67.4 67.0 | 67.2 | 4.6 4.6 | 4.6 | | | | | | | | | | | | | | | | | | 4.6 | 5.0 4.9 | 5.0 | 5.0 4.9 |
| Surface | 1 | 28.1 28.2 | 28.2 | 8.6 8.6 | 8.6 | 29.3 29.2 | 29.3 | 105.8 105.9 | 105.9 | 7.0 7.0 | 7.0 | 6.7 | 3.3 3.4 | 3.4 | 4.0 | 3.2 3.2 | 3.2 | 5.8 5.8 | 5.8 | | | | | | | | | | | | | |
| Middle | 4 | 27.7 27.7 | 27.7 | 8.6 8.6 | 8.6 | 29.6 29.6 | 29.6 | 96.4 96.5 | 96.5 | 6.4 6.4 | 6.4 | | | | | | | | | 5.3 | 3.4 3.6 | 3.5 | 4.0 | 5.1 5.0 | 5.1 | 3.8 3.7 | 3.8 | 3.8 | | | | |
| Bottom | 7 | 27.1 27.2 | 27.2 | 8.5 8.5 | 8.5 | 30.3 30.1 | 30.2 | 78.4 79.4 | 78.9 | 5.3 5.3 | 5.3 | | | | | | | | | | | | | | | | | | 6.1 | 3.2 3.2 | 3.2 | 4.0 |
| Surface | 1 | 27.5 27.4 | 27.5 | 8.6 8.5 | 8.6 | 29.7 29.8 | 29.8 | 97.2 88.2 | 92.7 | 6.5 5.9 | 6.2 | 5.3 | 3.2 3.2 | 3.2 | 4.0 | 3.2 3.2 | 3.2 | 4.7 4.7 | 4.7 | | | | | | | | | | | | | |
| Middle | 4.5 | 27.5 27.2 | 27.4 | 8.5 8.5 | 8.5 | 29.7 30.1 | 29.9 | 95.9 81.8 | 88.9 | 6.4 5.5 | 6.0 | | | | | | | | | 5.3 | 3.2 3.3 | 3.3 | 4.0 | 4.6 4.4 | 4.5 | 4.9 4.7 | 4.7 | 4.8 | | | | |
| Bottom | 8 | 27.1 27.1 | 27.1 | 8.5 8.5 | 8.5 | 30.4 30.4 | 30.4 | 77.2 79.9 | 78.6 | 5.2 5.4 | 5.3 | | | | | | | | | | | | | | | | | | 6.0 | 5.0 4.9 | 5.0 | 4.0 |
| Surface | 1 | 28.3 28.0 | 28.2 | 8.6 8.6 | 8.6 | 29.2 29.3 | 29.3 | 105.1 104.1 | 104.6 | 7.0 6.9 | 7.0 | 6.7 | 3.3 3.3 | 3.3 | 4.0 | 3.3 3.3 | 3.3 | 4.2 4.3 | 4.3 | | | | | | | | | | | | | |
| Middle | 4 | 27.6 27.0 | 27.3 | 8.5 8.5 | 8.5 | 29.7 30.0 | 29.9 | 94.8 94.6 | 94.7 | 6.3 6.4 | 6.4 | | | | | | | | | 6.0 | 3.7 3.6 | 3.7 | 4.0 | 5.0 4.9 | 5.0 | 3.1 3.1 | 3.1 | 3.1 | | | | |
| Bottom | 7 | 27.1 28.2 | 27.7 | 8.5 8.6 | 8.6 | 30.3 29.2 | 29.8 | 91.1 89.4 | 90.3 | 6.1 5.9 | 6.0 | | | | | | | | | | | | | | | | | | 6.9 | 3.3 3.4 | 3.4 | 4.0 |
| Surface | 1 | 28.0 28.2 | 28.1 | 8.6 8.6 | 8.6 | 29.6 29.5 | 29.6 | 107.4 108.3 | 107.9 | 7.1 7.2 | 7.2 | 6.9 | 3.2 3.1 | 3.2 | 4.0 | 3.2 3.1 | 3.2 | 3.6 3.6 | 3.6 | | | | | | | | | | | | | |
| Middle | 4.5 | 27.6 27.8 | 27.7 | 8.6 8.6 | 8.6 | 29.7 29.7 | 29.7 | 93.7 101.3 | 97.5 | 6.3 6.8 | 6.6 | | | | | | | | | 4.5 | 3.4 3.4 | 3.4 | 4.0 | 5.9 5.9 | 6.1 | 3.1 3.1 | 3.1 | 3.1 | | | | |
| Bottom | 8 | 26.9 26.8 | 26.9 | 8.4 8.4 | 8.4 | 30.2 30.3 | 30.3 | 65.9 66.0 | 66.0 | 4.4 4.5 | 4.5 | | | | | | | | | | | | | | | | | | 7.1 | 3.3 3.3 | 3.3 | 4.0 |
| Surface | 1 | 28.2 28.5 | 28.4 | 8.6 8.6 | 8.6 | 29.4 29.4 | 29.4 | 105.8 108.3 | 107.1 | 7.0 7.1 | 7.1 | 7.1 | 3.3 3.3 | 3.3 | 4.0 | 3.3 3.3 | 3.3 | 3.0 3.0 | 3.0 | | | | | | | | | | | | | |
| Middle | 3 | 28.1 28.0 | 28.1 | 8.6 8.6 | 8.6 | 29.5 29.5 | 29.5 | 106.0 103.7 | 104.9 | 7.0 6.9 | 7.0 | | | | | | | | | 6.3 | 3.4 3.4 | 3.4 | 4.0 | 3.4 3.4 | 3.4 | 3.1 3.1 | 3.1 | 3.1 | | | | |
| Bottom | 5 | 27.7 27.6 | 27.7 | 8.6 8.5 | 8.6 | 29.7 29.7 | 29.7 | 96.1 92.2 | 94.2 | 6.4 6.2 | 6.3 | | | | | | | | | | | | | | | | | | 6.3 | 3.8 3.9 | 3.9 | 4.0 |
| Surface | 1 | 28.6 28.6 | 28.6 | 8.6 8.6 | 8.6 | 29.5 29.4 | 29.5 | 109.9 109.8 | 109.9 | 7.2 7.2 | 7.2 | 6.8 | 3.1 3.1 | 3.1 | 4.0 | 3.1 3.1 | 3.1 | 5.3 5.3 | 5.3 | | | | | | | | | | | | | |
| Middle | 5.5 | 27.7 27.8 | 27.8 | 8.5 8.6 | 8.6 | 29.8 29.9 | 29.9 | 94.2 95.5 | 94.9 | 6.3 6.4 | 6.4 | | | | | | | | | 5.4 | 3.6 3.5 | 3.6 | 4.0 | 4.3 4.2 | 4.3 | 3.7 3.7 | 3.7 | 3.7 | | | | |
| Bottom | 10 | 27.1 27.2 | 27.2 | 8.4 8.5 | 8.5 | 30.4 30.5 | 30.5 | 79.2 79.8 | 79.5 | 5.3 5.4 | 5.4 | | | | | | | | | | | | | | | | | | 6.5 | 4.3 4.2 | 4.3 | 4.0 |
| Surface | 1 | 28.1 27.9 | 28.0 | 8.6 8.6 | 8.6 | 29.3 29.3 | 29.3 | 104.8 103.2 | 104.0 | 7.0 6.9 | 7.0 | 6.7 | 3.3 3.3 | 3.3 | 4.0 | 3.3 3.3 | 3.3 | 3.2 3.2 | 3.2 | | | | | | | | | | | | | |
| Middle | 4 | 27.6 27.7 | 27.7 | 8.5 8.6 | 8.6 | 29.5 29.4 | 29.5 | 94.8 96.5 | 95.7 | 6.3 6.5 | 6.4 | | | | | | | | | 6.5 | 3.5 3.6 | 3.6 | 4.0 | 6.5 6.5 | 6.5 | 3.6 3.6 | 3.6 | 3.6 | | | | |
| Bottom | 7 | 27.7 27.0 | 27.4 | 8.6 8.4 | 8.5 | 29.7 30.0 | 29.9 | 97.4 95.9 | 96.7 | 6.5 6.5 | 6.5 | | | | | | | | | | | | | | | | | | 6.5 | 5.2 5.3 | 5.3 | 4.0 |
| Surface | 1 | 28.6 28.6 | 28.6 | 8.6 8.6 | 8.6 | 29.5 29.4 | 29.5 | 109.0 109.3 | 109.2 | 7.2 7.2 | 7.2 | 6.8 | 3.0 3.1 | 3.1 | 4.0 | 3.0 3.1 | 3.1 | 4.4 4.3 | 4.4 | | | | | | | | | | | | | |
| Middle | 5 | 28.0 27.8 | 27.9 | 8.6 8.5 | 8.6 | 29.7 29.8 | 29.8 | 98.8 93.3 | 96.1 | 6.6 6.2 | 6.4 | | | | | | | | | 5.7 | 3.4 3.4 | 3.4 | 4.0 | 6.6 6.2 | 6.4 | 4.2 4.2 | 4.2 | 4.2 | | | | |
| Bottom | 9 | 27.4 27.3 | 27.4 | 8.5 8.5 | 8.5 | 30.2 30.3 | 30.3 | 84.2 85.2 | 84.7 | 5.6 5.7 | 5.7 | | | | | | | | | | | | | | | | | | 6.8 | 4.2 4.1 | 4.2 | 4.0 |
| Surface | 1 | 27.5 27.5 | 27.5 | 8.5 8.5 | 8.5 | 30.2 30.2 | 30.2 | 93.0 91.7 | 92.4 | 6.2 6.1 | 6.2 | 5.9 | 3.5 3.5 | 3.5 | 4.0 | 3.5 3.5 | 3.5 | 2.8 2.7 | 2.8 | | | | | | | | | | | | | |
| Middle | 6 | 27.1 27.1 | 27.1 | 8.5 8.5 | 8.5 | 30.6 30.6 | 30.6 | 83.8 84.1 | 84.0 | 5.6 5.6 | 5.6 | | | | | | | | | 4.3 | 3.4 3.4 | 3.4 | 4.0 | 4.4 4.3 | 4.3 | 3.7 3.7 | 3.7 | 3.7 | | | | |
| Bottom | 11 | 26.1 25.9 | 26.0 | 8.4 8.4 | 8.4 | 31.9 32.2 | 32.1 | 65.6 61.8 | 63.7 | 4.4 4.2 | 4.3 | | | | | | | | | | | | | | | | | | 6.1 | 4.3 4.3 | 4.3 | 4.0 |
| Surface | - | - | - | - | - | - | - | - | - | - | - | 6.1 | - | - | 6.0 | - | - | - | - | | | | | | | | | | | | | |
| Middle | 2.1 | 27.6 27.6 | 27.6 | 8.5 8.5 | 8.5 | 29.7 29.7 | 29.7 | 91.0 90.7 | 90.9 | 6.1 6.1 | 6.1 | | | | | | | | | 6.0 | 5.8 6.1 | 6.0 | 6.0 | 6.0 | 6.0 | 6.6 6.6 | 6.6 | 6.6 | | | | |
| Bottom | - | - | - | - | - | - | - | - | - | - | - | | | | | | | | | | | | | | | | | | 6.0 | - | - | 6.0 |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 9 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 6.1 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 6.6 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.4 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.4 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.1 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 11 October 2017**

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|------------|-------------------------|------------|------------|------------|--------------|------|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | | | |
| C1 | Sunny | Moderate | 16:03 | Surface | 1 | 29.7 29.5 | 29.6 | 8.3 8.3 | 8.3 | 33.5 33.6 | 33.6 | 93.9 92.8 | 93.4 | 5.9 5.9 | 5.9 | 5.9 | 4.0 | 3.0 3.2 | 3.1 | 4.9 4.8 | 4.9 | 5.4 | | |
| | | | | Middle | 9.5 | 29.4 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.7 33.7 | 33.7 | 92.8 92.6 | 92.7 | 5.9 5.9 | 5.9 | 5.9 | | 5.9 | 5.9 | 5.9 | 5.9 | | 5.9 | |
| | | | | Bottom | 18 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.9 33.9 | 33.9 | 90.2 90.0 | 90.1 | 5.7 5.7 | 5.7 | 5.7 | | 5.7 | 5.7 | 5.7 | 5.4 5.2 | | 5.4 5.3 | 5.3 |
| C2 | Sunny | Moderate | 15:01 | Surface | 1 | 29.6 29.6 | 29.6 | 8.2 8.3 | 8.3 | 33.6 33.6 | 33.6 | 92.8 92.7 | 92.8 | 5.9 5.9 | 5.9 | 5.9 | 3.3 3.3 | 3.3 | 5.1 5.1 | 5.1 | 5.3 | | | |
| | | | | Middle | 17 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.7 33.7 | 33.7 | 92.3 92.2 | 92.3 | 5.9 5.8 | 5.9 | | 5.9 | 5.9 | 5.9 | 5.9 | | 5.9 | 5.9 | |
| | | | | Bottom | 33 | 29.3 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.8 33.8 | 33.8 | 90.4 90.9 | 90.7 | 5.7 5.8 | 5.8 | | 5.8 | 5.8 | 5.8 | 5.3 4.9 | | 5.3 5.1 | 5.8 5.8 | 5.8 |
| G1 | Sunny | Moderate | 15:29 | Surface | 1 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 97.0 94.2 | 95.6 | 6.1 6.0 | 6.1 | 5.9 | 4.0 4.0 | 4.0 | 4.5 4.8 | 4.7 | 6.7 | | | |
| | | | | Middle | 4 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 89.0 87.7 | 88.4 | 5.7 5.6 | 5.7 | | 5.7 | 5.7 | 5.7 | 5.8 6.0 | | 5.9 | 11.3 11.2 | 11.3 |
| | | | | Bottom | 7 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.7 33.8 | 33.8 | 88.0 88.8 | 88.4 | 5.6 5.6 | 5.6 | | 5.6 | 5.6 | 5.6 | 5.2 5.3 | | 5.3 | 4.2 4.1 | 4.2 |
| G2 | Sunny | Moderate | 15:20 | Surface | 1 | 29.9 29.8 | 29.9 | 8.3 8.3 | 8.3 | 33.4 33.5 | 33.5 | 96.7 95.3 | 96.0 | 6.1 6.0 | 6.1 | 5.9 | 2.5 2.7 | 2.6 | 3.3 3.2 | 3.3 | 5.1 | | | |
| | | | | Middle | 5 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 87.9 88.4 | 88.2 | 5.6 5.6 | 5.6 | | 5.6 | 5.6 | 5.6 | 4.3 4.0 | | 4.2 | 6.1 6.1 | 6.1 |
| | | | | Bottom | 9 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.7 33.7 | 33.7 | 89.8 89.3 | 89.6 | 5.7 5.7 | 5.7 | | 5.7 | 5.7 | 5.7 | 3.9 3.8 | | 3.9 | 5.9 5.8 | 5.9 |
| G3 | Sunny | Moderate | 15:34 | Surface | 1 | 29.8 29.9 | 29.9 | 8.3 8.3 | 8.3 | 33.2 33.3 | 33.3 | 92.5 91.6 | 92.1 | 5.9 5.8 | 5.9 | 5.8 | 3.7 3.9 | 3.8 | 4.5 4.6 | 4.6 | 5.1 | | | |
| | | | | Middle | 4 | 29.7 29.6 | 29.7 | 8.3 8.3 | 8.3 | 33.4 33.5 | 33.5 | 90.4 89.6 | 90.0 | 5.7 5.7 | 5.7 | | 5.7 | 5.7 | 5.7 | 3.6 3.9 | | 3.8 | 5.9 6.0 | 6.0 |
| | | | | Bottom | 7 | 29.4 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 83.0 87.4 | 85.2 | 5.3 5.5 | 5.4 | | 5.4 | 5.4 | 5.4 | 4.6 4.6 | | 4.6 | 4.5 4.6 | 4.6 |
| G4 | Sunny | Moderate | 15:43 | Surface | 1 | 30.0 29.9 | 30.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 98.3 96.3 | 97.3 | 6.2 6.1 | 6.2 | 6.0 | 4.9 4.9 | 4.9 | 4.4 4.3 | 4.4 | 4.4 | | | |
| | | | | Middle | 4.5 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 92.4 91.7 | 92.1 | 5.8 5.8 | 5.8 | | 5.8 | 5.8 | 5.8 | 2.9 2.7 | | 2.8 | 4.7 4.7 | 4.7 |
| | | | | Bottom | 8 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 83.0 81.4 | 82.2 | 5.3 5.2 | 5.3 | | 5.3 | 5.3 | 5.3 | 5.2 5.3 | | 5.3 | 4.2 4.1 | 4.2 |
| M1 | Sunny | Moderate | 15:26 | Surface | 1 | 29.6 29.7 | 29.7 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 94.8 94.8 | 94.8 | 6.0 6.0 | 6.0 | 5.9 | 3.3 3.4 | 3.4 | 5.8 5.7 | 5.8 | 6.4 | | | |
| | | | | Middle | 3 | 29.5 29.6 | 29.6 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 89.3 89.7 | 89.5 | 5.7 5.7 | 5.7 | | 5.7 | 5.7 | 5.7 | 5.0 | | 5.4 | 8.7 8.6 | 8.7 |
| | | | | Bottom | 5 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 87.6 88.1 | 87.9 | 5.6 5.6 | 5.6 | | 5.6 | 5.6 | 5.6 | 5.1 5.1 | | 5.1 | 4.7 4.7 | 4.7 |
| M2 | Sunny | Moderate | 15:14 | Surface | 1 | 29.8 29.8 | 29.8 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 96.8 95.0 | 95.9 | 6.1 6.0 | 6.1 | 6.0 | 3.6 3.6 | 3.6 | 4.3 4.2 | 4.3 | 4.4 | | | |
| | | | | Middle | 6 | 29.4 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.7 33.6 | 33.7 | 91.1 91.0 | 91.1 | 5.8 5.8 | 5.8 | | 5.8 | 5.8 | 5.8 | 2.9 3.0 | | 3.0 | 4.6 4.5 | 4.6 |
| | | | | Bottom | 11 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.8 33.8 | 33.8 | 90.1 89.8 | 90.0 | 5.7 5.7 | 5.7 | | 5.7 | 5.7 | 5.7 | 5.2 5.3 | | 5.3 | 4.3 4.2 | 4.3 |
| M3 | Sunny | Moderate | 15:38 | Surface | 1 | 29.7 29.7 | 29.7 | 8.3 8.3 | 8.3 | 33.1 33.3 | 33.2 | 89.5 90.0 | 89.8 | 5.7 5.7 | 5.7 | 5.7 | 3.1 3.1 | 3.1 | 5.8 5.9 | 5.9 | 5.7 | | | |
| | | | | Middle | 4 | 29.6 29.7 | 29.7 | 8.3 8.3 | 8.3 | 33.5 33.4 | 33.5 | 89.8 90.3 | 90.1 | 5.7 5.7 | 5.7 | | 5.7 | 5.7 | 5.7 | 3.5 3.2 | | 3.4 | 5.3 5.2 | 5.3 |
| | | | | Bottom | 7 | 29.4 29.6 | 29.5 | 8.3 8.3 | 8.3 | 33.6 33.5 | 33.6 | 83.5 84.6 | 84.1 | 5.3 5.4 | 5.4 | | 5.4 | 5.4 | 5.4 | 3.9 3.9 | | 3.9 | 5.9 5.9 | 5.9 |
| M4 | Sunny | Moderate | 15:07 | Surface | 1 | 29.6 29.7 | 29.7 | 8.3 8.3 | 8.3 | 33.6 33.5 | 33.6 | 95.3 93.8 | 94.6 | 6.0 5.9 | 6.0 | 6.0 | 2.9 2.9 | 2.9 | 3.6 3.7 | 3.7 | 4.2 | | | |
| | | | | Middle | 5 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.7 33.7 | 33.7 | 92.9 92.6 | 92.8 | 5.9 5.9 | 5.9 | | 5.9 | 5.9 | 5.9 | 2.8 2.9 | | 2.9 | 3.8 3.9 | 3.9 |
| | | | | Bottom | 9 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.7 33.7 | 33.7 | 92.6 92.3 | 92.5 | 5.9 5.9 | 5.9 | | 5.9 | 5.9 | 5.9 | 2.8 2.8 | | 2.8 | 5.0 5.1 | 5.1 |
| M5 | Sunny | Moderate | 15:55 | Surface | 1 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 89.9 88.7 | 89.3 | 5.7 5.6 | 5.7 | 5.7 | 6.1 5.8 | 6.0 | 4.6 4.7 | 4.7 | 6.7 | | | |
| | | | | Middle | 6 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.7 33.7 | 33.7 | 88.8 88.3 | 88.6 | 5.6 5.6 | 5.6 | | 5.6 | 5.6 | 5.6 | 7.4 6.2 | | 6.8 | 9.2 9.1 | 9.2 |
| | | | | Bottom | 11 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.8 33.8 | 33.8 | 88.9 88.5 | 88.7 | 5.7 5.6 | 5.7 | | 5.7 | 5.7 | 5.7 | 6.1 6.1 | | 6.1 | 6.2 6.2 | 6.2 |
| M6 | Sunny | Moderate | 15:49 | Surface | - | - | - | - | - | - | - | - | - | - | - | 5.8 | - | - | - | - | 5.7 | | | |
| | | | | Middle | 2 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 91.8 91.5 | 91.7 | 5.8 5.8 | 5.8 | | 5.8 | 5.8 | 5.8 | 3.3 3.4 | | 3.4 | 5.7 5.6 | 5.7 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | | - | - | - | - | | - | - | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 11 October 2017 (Mid-Ebb Tide)

| <u>Parameter</u> <u>(unit)</u> | <u>Depth</u> | <u>Action Level</u> | <u>Limit Level</u> |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 6.1 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 6.6 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.1 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.1 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.0 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.5 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 11 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 11:41 | Surface | 1 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 91.6 91.5 | 91.6 | 5.8 5.8 | 5.8 | 5.8 | 3.0 3.0 | 3.0 | 5.0 | 4.9 4.9 | 4.9 | 5.6 |
| | | | | Middle | 9 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.7 33.7 | 33.7 | 91.2 91.1 | 91.2 | 5.8 5.8 | 5.8 | | 3.0 3.0 | 3.0 | | 5.3 5.2 | 5.3 | |
| | | | | Bottom | 17 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.9 33.9 | 33.9 | 90.1 90.3 | 90.2 | 5.7 5.7 | 5.7 | | 9.7 8.4 | 9.1 | | 6.7 6.6 | 6.7 | |
| C2 | Sunny | Moderate | 10:41 | Surface | 1 | 29.6 29.6 | 29.6 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.1 89.6 | 90.9 | 5.8 5.7 | 5.8 | 5.7 | 3.5 3.4 | 3.5 | 3.1 | 4.6 4.6 | 4.6 | 4.9 |
| | | | | Middle | 17 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 87.6 87.5 | 87.6 | 5.6 5.6 | 5.6 | | 2.9 2.9 | 2.9 | | 6.4 6.3 | 6.4 | |
| | | | | Bottom | 33 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.5 33.6 | 33.6 | 87.5 87.6 | 87.6 | 5.6 5.6 | 5.6 | | 2.9 2.9 | 2.9 | | 3.6 3.7 | 3.7 | |
| G1 | Sunny | Moderate | 11:08 | Surface | 1 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 89.3 88.7 | 89.0 | 5.7 5.6 | 5.7 | 5.7 | 3.9 3.8 | 3.9 | 3.4 | 5.4 5.3 | 5.4 | 5.2 |
| | | | | Middle | 4 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 90.3 89.2 | 89.8 | 5.7 5.7 | 5.7 | | 2.9 3.4 | 3.2 | | 4.8 4.9 | 4.9 | |
| | | | | Bottom | 7 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.6 33.5 | 33.6 | 87.8 88.8 | 88.3 | 5.6 5.6 | 5.6 | | 3.2 3.2 | 3.2 | | 5.1 5.2 | 5.2 | |
| G2 | Sunny | Moderate | 11:00 | Surface | 1 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 92.1 90.8 | 91.5 | 5.8 5.8 | 5.8 | 5.8 | 3.1 3.2 | 3.2 | 3.2 | 5.0 5.0 | 5.0 | 4.5 |
| | | | | Middle | 5 | 29.4 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 89.8 90.0 | 89.9 | 5.7 5.7 | 5.7 | | 3.3 3.1 | 3.2 | | 4.6 4.5 | 4.6 | |
| | | | | Bottom | 9 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 88.4 87.7 | 88.1 | 5.6 5.6 | 5.6 | | 3.0 3.1 | 3.1 | | 3.8 3.8 | 3.8 | |
| G3 | Sunny | Moderate | 11:14 | Surface | 1 | 29.4 29.3 | 29.4 | 8.3 8.3 | 8.3 | 33.1 33.6 | 33.4 | 87.7 85.8 | 86.8 | 5.6 5.5 | 5.6 | 5.6 | 2.7 3.3 | 3.0 | 3.3 | 5.6 5.7 | 5.7 | 5.4 |
| | | | | Middle | 4 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.6 33.5 | 33.6 | 88.2 87.4 | 87.8 | 5.6 5.6 | 5.6 | | 3.2 2.9 | 3.1 | | 5.0 4.9 | 5.0 | |
| | | | | Bottom | 7 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.7 33.7 | 33.7 | 82.6 85.8 | 84.2 | 5.3 5.5 | 5.4 | | 3.6 3.7 | 3.7 | | 5.6 5.5 | 5.6 | |
| G4 | Sunny | Moderate | 11:24 | Surface | 1 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 89.5 86.9 | 88.2 | 5.7 5.5 | 5.6 | 5.6 | 2.8 2.9 | 2.9 | 4.0 | 4.2 4.1 | 4.2 | 4.8 |
| | | | | Middle | 4.5 | 29.4 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 86.7 86.6 | 86.7 | 5.5 5.5 | 5.5 | | 3.0 2.9 | 3.0 | | 6.3 6.1 | 6.2 | |
| | | | | Bottom | 8 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.6 33.7 | 33.7 | 81.2 83.3 | 82.3 | 5.2 5.3 | 5.3 | | 5.5 6.5 | 6.0 | | 4.1 4.0 | 4.1 | |
| M1 | Sunny | Moderate | 11:04 | Surface | 1 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.5 33.6 | 33.6 | 91.3 89.6 | 90.5 | 5.8 5.7 | 5.8 | 5.8 | 3.2 3.2 | 3.2 | 3.2 | 4.0 4.1 | 4.1 | 4.7 |
| | | | | Middle | 3 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 90.3 89.9 | 90.1 | 5.7 5.7 | 5.7 | | 3.1 3.1 | 3.1 | | 4.8 4.9 | 4.9 | |
| | | | | Bottom | 5 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.7 33.7 | 33.7 | 89.9 89.6 | 89.8 | 5.7 5.7 | 5.7 | | 3.2 3.3 | 3.3 | | 4.9 5.0 | 5.0 | |
| M2 | Sunny | Moderate | 10:55 | Surface | 1 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 89.7 88.9 | 89.3 | 5.7 5.6 | 5.7 | 5.7 | 4.0 3.9 | 4.0 | 3.8 | 5.5 5.6 | 5.6 | 5.9 |
| | | | | Middle | 6 | 29.3 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 88.2 88.5 | 88.4 | 5.6 5.6 | 5.6 | | 3.7 3.8 | 3.8 | | 6.8 6.8 | 6.8 | |
| | | | | Bottom | 11 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 86.9 87.1 | 87.0 | 5.5 5.5 | 5.5 | | 3.8 3.3 | 3.6 | | 5.3 5.3 | 5.3 | |
| M3 | Sunny | Moderate | 11:18 | Surface | 1 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 32.8 33.2 | 33.0 | 89.6 86.7 | 88.2 | 5.7 5.5 | 5.6 | 5.6 | 3.5 3.1 | 3.3 | 3.2 | 2.6 2.5 | 2.6 | 4.0 |
| | | | | Middle | 4 | 29.4 29.4 | 29.4 | 8.3 8.3 | 8.3 | 33.2 33.6 | 33.4 | 87.3 86.1 | 86.7 | 5.6 5.5 | 5.6 | | 3.0 3.2 | 3.1 | | 3.9 4.0 | 4.0 | |
| | | | | Bottom | 7 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.7 33.6 | 33.7 | 85.5 86.8 | 86.2 | 5.4 5.5 | 5.5 | | 3.1 3.4 | 3.3 | | 5.3 5.4 | 5.4 | |
| M4 | Sunny | Moderate | 10:48 | Surface | 1 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 88.9 87.5 | 88.2 | 5.7 5.6 | 5.7 | 5.6 | 7.0 7.7 | 7.4 | 8.1 | 5.5 5.6 | 5.6 | 4.4 |
| | | | | Middle | 5 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 87.1 86.8 | 87.0 | 5.5 5.5 | 5.5 | | 8.3 8.4 | 8.4 | | 3.1 3.0 | 3.1 | |
| | | | | Bottom | 9 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 86.6 86.6 | 86.6 | 5.5 5.5 | 5.5 | | 8.1 8.7 | 8.4 | | 4.6 4.5 | 4.6 | |
| M5 | Sunny | Moderate | 11:35 | Surface | 1 | 29.4 29.3 | 29.4 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 89.0 87.9 | 88.5 | 5.7 5.6 | 5.7 | 5.6 | 3.7 3.9 | 3.8 | 7.1 | 4.4 4.5 | 4.5 | 6.6 |
| | | | | Middle | 6 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 86.8 86.9 | 86.9 | 5.5 5.5 | 5.5 | | 7.6 7.5 | 7.6 | | 9.8 9.9 | 9.9 | |
| | | | | Bottom | 11 | 29.3 29.3 | 29.3 | 8.3 8.3 | 8.3 | 33.8 33.8 | 33.8 | 90.1 90.4 | 90.3 | 5.7 5.7 | 5.7 | | 9.9 9.7 | 9.8 | | 5.2 5.4 | 5.3 | |
| M6 | Sunny | Moderate | 11:30 | Surface | - | - | - | - | - | - | - | - | - | - | 5.8 | - | - | 3.3 | - | - | 4.8 | |
| | | | | Middle | 2.1 | 29.5 29.5 | 29.5 | 8.3 8.3 | 8.3 | 33.5 33.4 | 33.5 | 90.9 90.1 | 90.5 | 5.8 5.7 | | 5.8 | 3.1 3.4 | | 3.3 | 4.9 4.7 | | 4.8 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 11 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|--|--|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 11.0 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 11.8 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 8.0 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 8.7 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 14 October 2017**

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | |
|----------|-------------------|-----------------|---------------|-----------|-----|------------------|---------|-------|---------|--------------|---------|-------------------|---------|-------------------------|---------|-----|----------------|---------|-----|-------------------------|---------|-----|
| | | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* |
| C1 | Sunny | Moderate | 09:17 | Surface | 1 | 28.9 | 28.9 | 8.3 | 8.3 | 33.4 | 33.4 | 91.8 | 91.8 | 5.9 | 5.9 | 5.9 | 2.6 | 2.7 | 4.3 | 4.8 | 4.9 | 5.6 |
| | | | | Middle | 10 | 28.9 | 28.9 | 8.3 | 8.3 | 33.4 | 33.4 | 91.8 | 91.9 | 5.9 | 5.9 | 4.6 | 4.7 | 4.7 | | 7.2 | 7.1 | |
| | | | | Bottom | 19 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 92.0 | 92.0 | 5.9 | 5.9 | 5.5 | 5.6 | 5.6 | | 4.8 | 4.8 | |
| C2 | Sunny | Moderate | 07:02 | Surface | 1 | 28.9 | 28.9 | 8.2 | 8.3 | 33.5 | 33.5 | 91.7 | 91.3 | 5.9 | 5.9 | 5.9 | 3.7 | 3.3 | 4.5 | 5.4 | 5.5 | 6.4 |
| | | | | Middle | 17 | 28.9 | 29.0 | 8.3 | 8.3 | 33.6 | 33.6 | 91.6 | 91.1 | 5.9 | 5.9 | 3.4 | 4.1 | 3.8 | | 7.6 | 8.0 | |
| | | | | Bottom | 33 | 28.9 | 28.9 | 8.3 | 8.3 | 33.6 | 33.6 | 91.4 | 91.2 | 5.8 | 5.8 | 6.2 | 6.3 | 6.3 | | 5.8 | 5.8 | |
| G1 | Sunny | Moderate | 07:58 | Surface | 1 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.6 | 91.5 | 5.9 | 5.9 | 5.9 | 3.1 | 3.1 | 3.1 | 3.1 | 3.2 | 5.2 |
| | | | | Middle | 4 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.8 | 91.3 | 5.9 | 5.9 | 3.0 | 3.1 | 3.1 | | 6.6 | 6.9 | |
| | | | | Bottom | 7 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.6 | 91.2 | 5.9 | 5.9 | 2.9 | 3.0 | 3.0 | | 5.6 | 5.5 | |
| G2 | Sunny | Moderate | 07:27 | Surface | 1 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.1 | 91.1 | 5.8 | 5.8 | 5.8 | 3.4 | 3.4 | 3.4 | 3.1 | 3.1 | 4.6 |
| | | | | Middle | 4.5 | 29.0 | 29.0 | 8.3 | 8.3 | 33.5 | 33.5 | 90.8 | 91.0 | 5.8 | 5.8 | 3.4 | 3.5 | 3.5 | | 5.9 | 6.0 | |
| | | | | Bottom | 8 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 90.8 | 91.4 | 5.8 | 5.9 | 3.3 | 3.1 | 3.2 | | 4.8 | 4.8 | |
| G3 | Sunny | Moderate | 08:12 | Surface | 1 | 28.9 | 28.9 | 8.3 | 8.3 | 33.4 | 33.4 | 91.1 | 90.5 | 5.8 | 5.8 | 5.8 | 3.1 | 3.2 | 3.1 | 3.1 | 3.2 | 4.9 |
| | | | | Middle | 4 | 28.9 | 28.9 | 8.3 | 8.3 | 33.4 | 33.4 | 91.0 | 90.9 | 5.8 | 5.8 | 3.0 | 3.0 | 3.0 | | 7.0 | 7.2 | |
| | | | | Bottom | 7 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.6 | 90.9 | 5.9 | 5.9 | 2.9 | 3.0 | 3.0 | | 4.2 | 4.5 | |
| G4 | Sunny | Moderate | 08:44 | Surface | 1 | 28.9 | 28.9 | 8.3 | 8.3 | 33.4 | 33.4 | 91.4 | 91.3 | 5.9 | 5.9 | 5.9 | 2.9 | 2.9 | 2.8 | 5.3 | 5.2 | 5.0 |
| | | | | Middle | 4.5 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.6 | 91.3 | 5.9 | 5.9 | 2.8 | 2.9 | 2.9 | | 5.3 | 5.2 | |
| | | | | Bottom | 8 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.5 | 91.8 | 5.9 | 5.9 | 2.7 | 2.6 | 2.7 | | 4.4 | 4.6 | |
| M1 | Sunny | Moderate | 07:46 | Surface | 1 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.7 | 92.0 | 5.9 | 5.9 | 5.9 | 3.2 | 3.1 | 3.0 | 4.8 | 4.9 | 5.9 |
| | | | | Middle | 3 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.7 | 92.2 | 5.9 | 5.9 | 3.0 | 3.0 | 3.0 | | 7.3 | 7.4 | |
| | | | | Bottom | 5 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.8 | 92.3 | 5.9 | 5.9 | 3.0 | 2.8 | 2.9 | | 5.4 | 5.5 | |
| M2 | Sunny | Moderate | 07:19 | Surface | 1 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 92.6 | 91.2 | 5.9 | 5.9 | 5.9 | 3.4 | 3.4 | 3.3 | 4.7 | 4.8 | 6.2 |
| | | | | Middle | 6 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.5 | 91.3 | 5.9 | 5.9 | 3.3 | 3.4 | 3.4 | | 7.5 | 7.6 | |
| | | | | Bottom | 11 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.7 | 91.5 | 5.9 | 5.9 | 2.9 | 3.0 | 3.0 | | 6.2 | 6.2 | |
| M3 | Sunny | Moderate | 08:26 | Surface | 1 | 28.9 | 28.9 | 8.3 | 8.3 | 33.4 | 33.4 | 90.9 | 91.2 | 5.8 | 5.8 | 5.8 | 3.0 | 3.1 | 2.9 | 4.7 | 4.7 | 4.9 |
| | | | | Middle | 4 | 28.9 | 28.9 | 8.3 | 8.3 | 33.4 | 33.4 | 91.0 | 91.1 | 5.8 | 5.8 | 2.9 | 2.9 | 2.9 | | 5.2 | 5.4 | |
| | | | | Bottom | 7 | 28.9 | 28.9 | 8.3 | 8.3 | 33.4 | 33.5 | 91.3 | 91.5 | 5.8 | 5.9 | 2.7 | 2.7 | 2.7 | | 4.4 | 4.5 | |
| M4 | Sunny | Moderate | 07:13 | Surface | 1 | 29.0 | 29.0 | 8.3 | 8.3 | 33.5 | 33.5 | 91.2 | 91.3 | 5.8 | 5.8 | 5.8 | 3.3 | 3.3 | 4.1 | 5.0 | 5.1 | 4.7 |
| | | | | Middle | 5.5 | 29.0 | 29.0 | 8.3 | 8.3 | 33.5 | 33.5 | 91.2 | 91.2 | 5.8 | 5.8 | 3.2 | 3.2 | 3.2 | | 4.7 | 4.8 | |
| | | | | Bottom | 10 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 91.1 | 91.1 | 5.8 | 5.8 | 3.1 | 3.1 | 5.9 | | 4.4 | 4.3 | |
| M5 | Sunny | Moderate | 09:07 | Surface | 1 | 28.9 | 28.9 | 8.3 | 8.3 | 33.4 | 33.4 | 92.0 | 91.8 | 5.9 | 5.9 | 5.9 | 2.7 | 2.8 | 2.7 | 4.6 | 4.6 | 4.8 |
| | | | | Middle | 6 | 28.9 | 28.9 | 8.3 | 8.3 | 33.4 | 33.4 | 91.9 | 91.7 | 5.9 | 5.9 | 2.7 | 2.6 | 2.7 | | 5.0 | 4.9 | |
| | | | | Bottom | 11 | 28.9 | 28.9 | 8.4 | 8.4 | 33.5 | 33.5 | 92.5 | 92.3 | 5.9 | 5.9 | 2.4 | 2.6 | 2.5 | | 4.9 | 4.9 | |
| M6 | Sunny | Moderate | 09:00 | Surface | - | - | - | - | - | - | - | - | - | - | - | - | - | - | 2.6 | - | - | 6.2 |
| | | | | Middle | 1.5 | 28.9 | 28.9 | 8.3 | 8.3 | 33.5 | 33.5 | 92.1 | 92.1 | 5.9 | 5.9 | 2.6 | 2.5 | 2.6 | | 6.2 | 6.1 | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | - | - | - | | - | - | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 14 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 7.6 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 8.2 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.0 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.5 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 14 October 2017

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|------------|-------------------------|------------|------------|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 15:38 | Surface | 1 | 28.8 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.6 92.5 | 92.6 | 5.9 5.9 | 5.9 | 5.9 | 4.9 | 2.5 2.6 | 2.6 | 5.7 | 4.8 4.8 | 4.8 |
| | | | | Middle | 10 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.3 92.0 | 92.2 | 5.9 5.9 | 5.9 | 5.9 | | 5.6 5.6 | 5.6 | | 6.7 6.6 | 6.7 |
| | | | | Bottom | 19 | 28.7 28.7 | 28.7 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 92.9 92.9 | 92.9 | 6.0 6.0 | 6.0 | 6.0 | | 6.6 6.5 | 6.6 | | 5.7 5.6 | 5.7 |
| C2 | Sunny | Moderate | 13:52 | Surface | 1 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 91.9 92.0 | 92.0 | 5.9 5.9 | 5.9 | 4.2 | 2.6 2.6 | 2.6 | 4.9 | 3.6 3.6 | 3.5 | |
| | | | | Middle | 17 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 91.9 92.0 | 92.0 | 5.9 5.9 | 5.9 | | 5.9 | 3.6 3.6 | | 3.6 | 5.1 5.1 | 5.1 |
| | | | | Bottom | 33 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 92.4 92.2 | 92.3 | 5.9 5.9 | 5.9 | | 5.9 | 6.5 6.5 | | 6.5 | 6.0 6.1 | 6.1 |
| G1 | Sunny | Moderate | 14:45 | Surface | 1 | 28.8 28.8 | 28.8 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.2 92.2 | 92.2 | 5.9 5.9 | 5.9 | 2.6 | 2.6 2.5 | 2.6 | 5.7 | 5.4 5.6 | 5.5 | |
| | | | | Middle | 4 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.0 92.1 | 92.1 | 5.9 5.9 | 5.9 | | 5.9 | 2.5 2.6 | | 2.6 | 6.8 6.7 | 6.8 |
| | | | | Bottom | 7 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.0 92.0 | 92.0 | 5.9 5.9 | 5.9 | | 5.9 | 2.6 2.7 | | 2.7 | 4.9 4.9 | 4.9 |
| G2 | Sunny | Moderate | 14:21 | Surface | 1 | 28.9 28.8 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.1 92.1 | 92.1 | 5.9 5.9 | 5.9 | 2.6 | 2.5 2.5 | 2.5 | 5.0 | 4.8 4.8 | 4.8 | |
| | | | | Middle | 4.5 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.0 92.1 | 92.1 | 5.9 5.9 | 5.9 | | 5.9 | 2.5 2.6 | | 2.6 | 5.3 5.1 | 5.2 |
| | | | | Bottom | 8 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.5 | 33.5 | 91.9 92.0 | 92.0 | 5.9 5.9 | 5.9 | | 5.9 | 2.8 2.7 | | 2.8 | 5.0 5.1 | 5.1 |
| G3 | Sunny | Moderate | 14:52 | Surface | 1 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.3 92.4 | 92.4 | 5.9 5.9 | 5.9 | 2.7 | 2.7 2.5 | 2.6 | 5.0 | 5.2 5.1 | 5.2 | |
| | | | | Middle | 4 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.3 92.3 | 92.3 | 5.9 5.9 | 5.9 | | 5.9 | 2.7 2.6 | | 2.7 | 5.0 5.1 | 5.1 |
| | | | | Bottom | 7 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.2 92.0 | 92.1 | 5.9 5.9 | 5.9 | | 5.9 | 2.6 2.8 | | 2.7 | 4.6 4.5 | 4.6 |
| G4 | Sunny | Moderate | 15:13 | Surface | 1 | 28.9 28.8 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.5 92.6 | 92.6 | 5.9 5.9 | 5.9 | 2.6 | 2.6 2.5 | 2.6 | 5.3 | 3.6 3.5 | 3.6 | |
| | | | | Middle | 4.5 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.3 92.1 | 92.2 | 5.9 5.9 | 5.9 | | 5.9 | 2.5 2.5 | | 2.5 | 5.6 5.5 | 5.6 |
| | | | | Bottom | 8 | 28.8 28.8 | 28.8 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 91.9 91.9 | 91.9 | 5.9 5.9 | 5.9 | | 5.9 | 2.7 2.7 | | 2.7 | 6.6 6.6 | 6.6 |
| M1 | Sunny | Moderate | 14:38 | Surface | 1 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.1 92.0 | 92.1 | 5.9 5.9 | 5.9 | 2.6 | 2.5 2.6 | 2.6 | 5.5 | 3.4 3.5 | 3.5 | |
| | | | | Middle | 3.5 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.1 92.1 | 92.1 | 5.9 5.9 | 5.9 | | 5.9 | 2.5 2.7 | | 2.6 | 7.1 7.3 | 7.2 |
| | | | | Bottom | 6 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.5 | 33.5 | 92.0 92.0 | 92.0 | 5.9 5.9 | 5.9 | | 5.9 | 2.6 2.6 | | 2.6 | 5.9 5.8 | 5.9 |
| M2 | Sunny | Moderate | 14:08 | Surface | 1 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.1 92.1 | 92.1 | 5.9 5.9 | 5.9 | 2.6 | 2.5 2.5 | 2.5 | 6.2 | 5.7 5.7 | 5.7 | |
| | | | | Middle | 6 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.1 92.1 | 92.1 | 5.9 5.9 | 5.9 | | 5.9 | 2.7 2.6 | | 2.7 | 6.7 6.8 | 6.8 |
| | | | | Bottom | 11 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.5 33.4 | 33.5 | 92.0 92.0 | 92.0 | 5.9 5.9 | 5.9 | | 5.9 | 2.6 2.5 | | 2.6 | 6.1 5.9 | 6.0 |
| M3 | Sunny | Moderate | 15:02 | Surface | 1 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.5 | 33.5 | 91.1 91.6 | 91.4 | 5.8 5.9 | 5.9 | 2.9 | 3.1 3.1 | 3.1 | 6.1 | 5.3 5.5 | 5.4 | |
| | | | | Middle | 4 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 91.0 91.0 | 91.0 | 5.8 5.8 | 5.8 | | 5.8 | 2.9 2.9 | | 2.9 | 6.2 6.1 | 6.2 |
| | | | | Bottom | 7 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 91.8 91.7 | 91.8 | 5.9 5.9 | 5.9 | | 5.9 | 2.6 2.6 | | 2.6 | 6.6 6.8 | 6.7 |
| M4 | Sunny | Moderate | 14:01 | Surface | 1 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.0 92.0 | 92.0 | 5.9 5.9 | 5.9 | 2.6 | 2.6 2.6 | 2.6 | 4.4 | 4.4 4.6 | 4.5 | |
| | | | | Middle | 5.5 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.0 91.9 | 92.0 | 5.9 5.9 | 5.9 | | 5.9 | 2.5 2.6 | | 2.6 | 4.2 4.2 | 4.2 |
| | | | | Bottom | 10 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 91.8 92.0 | 91.9 | 5.9 5.9 | 5.9 | | 5.9 | 2.5 2.8 | | 2.7 | 4.6 4.6 | 4.6 |
| M5 | Sunny | Moderate | 15:29 | Surface | 1 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.2 92.2 | 92.2 | 5.9 5.9 | 5.9 | 2.7 | 2.6 2.6 | 2.6 | 5.3 | 3.5 3.5 | 3.5 | |
| | | | | Middle | 6 | 28.9 28.9 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.4 | 33.4 | 92.3 92.0 | 92.2 | 5.9 5.9 | 5.9 | | 5.9 | 2.5 2.8 | | 2.7 | 7.6 7.9 | 7.8 |
| | | | | Bottom | 11 | 28.9 28.8 | 28.9 | 8.3 8.3 | 8.3 | 33.4 33.5 | 33.5 | 92.0 92.0 | 92.0 | 5.9 5.9 | 5.9 | | 5.9 | 2.7 2.6 | | 2.7 | 4.4 4.6 | 4.5 |
| M6 | Sunny | Moderate | 15:21 | Surface | - | - | - | - | - | - | - | - | - | - | 3.1 | - | - | 5.5 | - | - | | |
| | | | | Middle | 1.4 | 28.9 29.0 | 29.0 | 8.3 8.3 | 8.3 | 33.4 33.5 | 33.5 | 92.1 91.2 | 91.7 | 5.9 5.8 | | 5.9 | 5.9 | | 2.8 3.4 | 3.1 | 5.5 5.5 | 5.5 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | - | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 14 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 8.0 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 8.6 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.8 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.2 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.8 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.2 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.8 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.4 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 16 October 2017**

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|--------------|-------------------------|------------|------------|------------|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | | |
| C1 | Rainy | Rough | 11:13 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.2 94.2 | 94.2 | 6.1 6.1 | 6.1 | 6.1 | 6.1 | 6.9 6.9 | 6.9 | 7.2 | 5.0 5.2 | 5.1 | 5.8 |
| | | | | Middle | 10 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.2 93.2 | 93.2 | 6.1 6.1 | 6.1 | 6.1 | | 7.2 7.2 | 7.2 | | 7.2 | 7.2 | |
| | | | | Bottom | 19 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 92.9 92.8 | 92.9 | 6.0 6.0 | 6.0 | 6.0 | | 7.4 7.2 | 7.3 | | 7.3 | 5.2 4.7 | |
| C2 | Rainy | Rough | 09:09 | Surface | 1 | 28.0 28.0 | 28.0 | 8.3 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.4 94.0 | 94.2 | 6.1 6.1 | 6.1 | 6.1 | 7.9 7.3 | 7.6 | 8.8 | 5.3 5.1 | 5.2 | 4.7 | |
| | | | | Middle | 17.5 | 27.9 27.9 | 27.9 | 8.3 8.4 | 8.4 | 33.6 33.5 | 33.6 | 92.7 92.9 | 92.8 | 6.0 6.0 | 6.0 | | 6.0 | 8.9 8.6 | | 8.8 | 3.4 3.3 | | 3.4 |
| | | | | Bottom | 34 | 27.9 27.9 | 27.9 | 8.3 8.4 | 8.4 | 33.6 33.6 | 33.6 | 92.5 92.2 | 92.4 | 6.0 6.0 | 6.0 | | 6.0 | 9.9 9.8 | | 9.9 | 5.4 5.8 | | 5.6 |
| G1 | Rainy | Rough | 10:12 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.6 94.5 | 94.6 | 6.1 6.1 | 6.1 | 6.1 | 6.9 6.9 | 6.9 | 7.3 | 3.9 4.0 | 4.0 | 4.2 | |
| | | | | Middle | 4 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.0 93.9 | 94.0 | 6.1 6.1 | 6.1 | | 6.1 | 7.2 7.3 | | 7.3 | 4.5 4.4 | | 4.5 |
| | | | | Bottom | 7 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.6 93.6 | 93.6 | 6.1 6.1 | 6.1 | | 6.1 | 7.7 7.8 | | 7.8 | 4.2 3.9 | | 4.1 |
| G2 | Rainy | Rough | 09:47 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.1 94.1 | 94.1 | 6.1 6.1 | 6.1 | 6.1 | 7.3 7.4 | 7.4 | 7.6 | 3.9 3.8 | 3.9 | 3.7 | |
| | | | | Middle | 4.5 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.4 93.4 | 93.4 | 6.1 6.1 | 6.1 | | 6.1 | 7.4 7.3 | | 7.4 | 4.0 4.0 | | 4.0 |
| | | | | Bottom | 8 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.6 33.5 | 33.6 | 93.0 93.0 | 93.0 | 6.1 6.1 | 6.1 | | 6.1 | 7.9 7.8 | | 7.9 | 3.2 3.0 | | 3.1 |
| G3 | Rainy | Rough | 10:24 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.6 94.6 | 94.6 | 6.1 6.2 | 6.2 | 6.2 | 6.9 7.0 | 7.0 | 7.3 | 3.1 3.4 | 3.3 | 4.1 | |
| | | | | Middle | 4 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.2 94.1 | 94.2 | 6.1 6.1 | 6.1 | | 6.1 | 7.3 7.4 | | 7.4 | 5.1 5.1 | | 5.1 |
| | | | | Bottom | 7 | 27.9 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.7 93.7 | 93.7 | 6.1 6.1 | 6.1 | | 6.1 | 7.7 7.5 | | 7.6 | 3.8 4.2 | | 4.0 |
| G4 | Rainy | Rough | 10:51 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.3 94.3 | 94.3 | 6.1 6.1 | 6.1 | 6.1 | 7.3 7.3 | 7.3 | 7.5 | 4.7 4.6 | 4.7 | 4.4 | |
| | | | | Middle | 4.5 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.6 93.7 | 93.7 | 6.1 6.1 | 6.1 | | 6.1 | 7.5 7.5 | | 7.5 | 3.9 3.9 | | 3.9 |
| | | | | Bottom | 8 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.1 93.0 | 93.1 | 6.1 6.1 | 6.1 | | 6.1 | 7.6 7.6 | | 7.6 | 4.8 4.5 | | 4.7 |
| M1 | Rainy | Rough | 10:00 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.4 94.4 | 94.4 | 6.1 6.1 | 6.1 | 6.1 | 6.9 6.9 | 6.9 | 7.2 | 5.4 5.6 | 5.5 | 5.9 | |
| | | | | Middle | 3 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.9 93.9 | 93.9 | 6.1 6.1 | 6.1 | | 6.1 | 7.2 7.2 | | 7.2 | 6.6 6.6 | | 6.6 |
| | | | | Bottom | 5 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.6 93.6 | 93.6 | 6.1 6.1 | 6.1 | | 6.1 | 7.4 7.3 | | 7.4 | 5.4 5.5 | | 5.5 |
| M2 | Rainy | Rough | 09:35 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.0 93.9 | 94.0 | 6.1 6.1 | 6.1 | 6.1 | 8.4 8.0 | 8.2 | 8.5 | 4.8 5.1 | 5.0 | 4.9 | |
| | | | | Middle | 6 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 92.9 93.2 | 93.1 | 6.0 6.1 | 6.1 | | 6.1 | 8.7 7.9 | | 8.3 | 3.6 3.4 | | 3.5 |
| | | | | Bottom | 11 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 92.5 92.6 | 92.6 | 6.0 6.0 | 6.0 | | 6.0 | 9.3 8.6 | | 9.0 | 6.3 6.1 | | 6.2 |
| M3 | Rainy | Rough | 10:35 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.6 94.6 | 94.6 | 6.2 6.2 | 6.2 | 6.2 | 7.1 7.2 | 7.2 | 7.5 | 4.7 4.6 | 4.7 | 5.9 | |
| | | | | Middle | 4 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.1 93.9 | 94.0 | 6.1 6.1 | 6.1 | | 6.1 | 7.3 7.5 | | 7.4 | 7.8 7.9 | | 7.9 |
| | | | | Bottom | 7 | 28.0 27.9 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.6 93.3 | 93.5 | 6.1 6.1 | 6.1 | | 6.1 | 7.6 7.9 | | 7.8 | 5.2 4.7 | | 5.0 |
| M4 | Rainy | Rough | 09:24 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.0 93.9 | 94.0 | 6.1 6.1 | 6.1 | 6.1 | 8.2 8.3 | 8.3 | 9.4 | 5.3 5.2 | 5.3 | 6.5 | |
| | | | | Middle | 5.5 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 92.7 92.8 | 92.8 | 6.0 6.0 | 6.0 | | 6.0 | 9.4 9.3 | | 9.4 | 7.9 7.6 | | 7.8 |
| | | | | Bottom | 10 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 91.8 92.3 | 92.1 | 6.0 6.0 | 6.0 | | 6.0 | 10.7 10.2 | | 10.5 | 6.2 6.4 | | 6.3 |
| M5 | Rainy | Rough | 11:04 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.1 94.1 | 94.1 | 6.1 6.1 | 6.1 | 6.1 | 7.1 7.3 | 7.2 | 7.4 | 5.1 5.5 | 5.3 | 5.6 | |
| | | | | Middle | 6 | 27.9 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.5 93.5 | 93.5 | 6.1 6.1 | 6.1 | | 6.1 | 7.3 7.2 | | 7.3 | 7.8 7.6 | | 7.7 |
| | | | | Bottom | 11 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 92.4 92.4 | 92.4 | 6.0 6.0 | 6.0 | | 6.0 | 7.6 7.5 | | 7.6 | 3.7 3.9 | | 3.8 |
| M6 | Rainy | Rough | 11:01 | Surface | - | - | - | - | - | - | - | - | - | - | - | 6.1 | - | - | 7.2 | - | - | 2.6 | |
| | | | | Middle | 1.4 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.2 94.1 | 94.2 | 6.1 6.1 | 6.1 | | 6.1 | 7.2 7.1 | | 7.2 | 2.6 2.6 | | 2.6 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 16 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|--|--|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 11.9 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 12.9 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.2 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.8 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.2 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.8 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.7 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.3 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 16 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|--------------|------|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Cloudy | Rough | 16:52 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 94.0 93.9 | 94.0 | 6.1 6.1 | 6.1 | 6.1 | 6.1 6.1 | 6.1 | 6.7 | 4.3 4.5 | 4.4 | 6.3 |
| | | | | Middle | 9.5 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.4 93.3 | 93.4 | 6.1 6.1 | 6.1 | | 6.1 6.3 | 6.3 | | 10.2 10.0 | 10.1 | |
| | | | | Bottom | 18 | 27.9 27.9 | 27.9 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 91.5 91.8 | 91.7 | 6.0 6.0 | 6.0 | | 7.2 7.9 | 7.6 | | 4.5 4.3 | 4.4 | |
| C2 | Cloudy | Rough | 15:11 | Surface | 1 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.7 93.7 | 93.7 | 6.1 6.1 | 6.1 | 6.1 | 6.9 6.6 | 6.9 | 7.1 | 3.4 3.3 | 3.4 | 3.7 |
| | | | | Middle | 16.5 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.0 93.0 | 93.0 | 6.1 6.1 | 6.1 | | 7.2 7.1 | 7.2 | | 2.8 3.0 | 2.9 | |
| | | | | Bottom | 32 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 92.9 92.9 | 92.9 | 6.0 6.0 | 6.0 | | 7.2 7.2 | 7.2 | | 4.9 4.8 | 4.9 | |
| G1 | Cloudy | Rough | 16:05 | Surface | 1 | 28.0 28.0 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 93.4 93.5 | 93.5 | 6.1 6.1 | 6.1 | 6.1 | 7.3 7.3 | 7.3 | 7.5 | 4.4 4.2 | 4.3 | 4.9 |
| | | | | Middle | 3.5 | 28.0 27.9 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 92.8 92.8 | 92.8 | 6.0 6.0 | 6.0 | | 7.6 7.7 | 7.7 | | 5.7 5.7 | 5.7 | |
| | | | | Bottom | 6 | 27.9 27.9 | 27.9 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 91.7 91.7 | 91.7 | 6.0 6.0 | 6.0 | | 7.6 7.6 | 7.6 | | 4.6 4.6 | 4.6 | |
| G2 | Cloudy | Rough | 15:46 | Surface | 1 | 28.0 28.0 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 93.9 93.8 | 93.9 | 6.1 6.1 | 6.1 | 6.1 | 7.1 7.0 | 7.1 | 7.8 | 4.0 4.1 | 4.1 | 4.1 |
| | | | | Middle | 4 | 27.9 28.0 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 93.0 93.0 | 93.0 | 6.1 6.1 | 6.1 | | 7.9 7.7 | 7.8 | | 4.4 4.3 | 4.4 | |
| | | | | Bottom | 7 | 27.9 27.9 | 27.9 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 92.6 92.5 | 92.6 | 6.0 6.0 | 6.0 | | 8.9 8.0 | 8.5 | | 3.7 3.6 | 3.7 | |
| G3 | Cloudy | Rough | 16:13 | Surface | 1 | 28.0 28.0 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 93.5 93.6 | 93.6 | 6.1 6.1 | 6.1 | 6.1 | 7.0 6.9 | 7.0 | 7.7 | 5.1 4.8 | 5.0 | 6.4 |
| | | | | Middle | 3.5 | 28.0 28.0 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 93.0 92.9 | 93.0 | 6.0 6.0 | 6.0 | | 7.2 7.4 | 7.3 | | 9.8 9.7 | 9.8 | |
| | | | | Bottom | 6 | 27.9 27.9 | 27.9 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 91.6 91.8 | 91.7 | 6.0 6.0 | 6.0 | | 8.8 8.9 | 8.9 | | 4.4 4.6 | 4.5 | |
| G4 | Cloudy | Rough | 16:29 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.8 93.8 | 93.8 | 6.1 6.1 | 6.1 | 6.1 | 6.3 6.3 | 6.3 | 6.8 | 4.4 4.3 | 4.4 | 4.0 |
| | | | | Middle | 4 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.2 93.2 | 93.2 | 6.1 6.1 | 6.1 | | 6.4 6.5 | 6.5 | | 3.3 3.2 | 3.3 | |
| | | | | Bottom | 7 | 27.9 27.9 | 27.9 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 91.8 91.7 | 91.8 | 6.0 6.0 | 6.0 | | 7.8 7.6 | 7.7 | | 4.4 4.4 | 4.4 | |
| M1 | Cloudy | Rough | 15:56 | Surface | 1 | 28.0 27.9 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.6 | 33.6 | 93.1 92.6 | 92.9 | 6.1 6.0 | 6.1 | 6.1 | 7.6 8.9 | 8.3 | 7.8 | 3.7 3.7 | 3.7 | 4.6 |
| | | | | Middle | 3 | 27.9 28.0 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 92.6 93.1 | 92.9 | 6.0 6.1 | 6.1 | | 8.6 7.0 | 7.8 | | 6.0 6.3 | 6.2 | |
| | | | | Bottom | 5 | 28.0 28.0 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 92.8 92.8 | 92.8 | 6.0 6.0 | 6.0 | | 7.2 7.1 | 7.2 | | 4.0 3.9 | 4.0 | |
| M2 | Cloudy | Rough | 15:38 | Surface | 1 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.1 93.2 | 93.2 | 6.1 6.1 | 6.1 | 6.1 | 7.0 6.9 | 7.0 | 6.9 | 3.7 3.8 | 3.8 | 4.1 |
| | | | | Middle | 5 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.2 93.2 | 93.2 | 6.1 6.1 | 6.1 | | 6.9 6.9 | 6.9 | | 4.8 4.9 | 4.9 | |
| | | | | Bottom | 9 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 92.7 92.4 | 92.6 | 6.0 6.0 | 6.0 | | 6.9 6.9 | 6.9 | | 3.3 3.6 | 3.5 | |
| M3 | Cloudy | Rough | 16:21 | Surface | 1 | 28.0 28.0 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 93.7 93.7 | 93.7 | 6.1 6.1 | 6.1 | 6.1 | 6.5 6.5 | 6.5 | 7.3 | 3.8 3.5 | 3.7 | 3.5 |
| | | | | Middle | 3.5 | 28.0 28.0 | 28.0 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 93.1 93.3 | 93.2 | 6.1 6.1 | 6.1 | | 6.8 6.5 | 6.7 | | 3.8 3.7 | 3.8 | |
| | | | | Bottom | 6 | 27.9 27.9 | 27.9 | 8.3 8.3 | 8.3 | 33.6 33.6 | 33.6 | 92.0 91.9 | 92.0 | 6.0 6.0 | 6.0 | | 8.4 8.7 | 8.6 | | 3.1 3.1 | 3.1 | |
| M4 | Cloudy | Rough | 15:28 | Surface | 1 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.3 93.3 | 93.3 | 6.1 6.1 | 6.1 | 6.1 | 7.0 7.0 | 7.0 | 7.1 | 3.5 3.6 | 3.6 | 3.6 |
| | | | | Middle | 4.5 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.4 93.4 | 93.4 | 6.1 6.1 | 6.1 | | 7.0 6.9 | 7.0 | | 3.3 3.1 | 3.2 | |
| | | | | Bottom | 8 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 92.7 92.5 | 92.6 | 6.0 6.0 | 6.0 | | 7.2 7.1 | 7.2 | | 3.9 3.8 | 3.9 | |
| M5 | Cloudy | Rough | 16:43 | Surface | 1 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.8 93.7 | 93.8 | 6.1 6.1 | 6.1 | 6.1 | 6.1 6.2 | 6.2 | 6.4 | 4.0 4.1 | 4.1 | 4.2 |
| | | | | Middle | 5.5 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 93.6 93.5 | 93.6 | 6.1 6.1 | 6.1 | | 6.1 6.1 | 6.1 | | 3.8 3.9 | 3.9 | |
| | | | | Bottom | 10 | 28.0 28.0 | 28.0 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 92.9 93.0 | 93.0 | 6.0 6.1 | 6.1 | | 6.8 6.7 | 6.8 | | 4.7 4.5 | 4.6 | |
| M6 | Cloudy | Rough | 16:37 | Surface | - | - | - | - | - | - | - | - | - | - | 6.0 | - | - | 8.3 | - | - | 4.8 | |
| | | | | Middle | 2.3 | 27.9 27.9 | 27.9 | 8.3 8.3 | 8.3 | 33.5 33.5 | 33.5 | 92.3 92.4 | 92.4 | 6.0 6.0 | | 6.0 | 8.7 7.9 | | 8.3 | 4.6 4.9 | | 4.8 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 16 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|--|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 9.1 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 10.0 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.3 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.7 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.3 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.7 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.3 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.7 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 18 October 2017

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|----------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 11:59 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 103.2 101.1 | 102.2 | 6.8 6.7 | 6.8 | 6.3 | 3.7 3.8 | 3.8 | 5.0 | 5.2 5.9 | 5.6 | 6.2 |
| | | | | Middle | 10 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 86.7 88.4 | 87.6 | 5.7 5.8 | 5.8 | | 4.8 4.7 | 4.8 | | 4.9 8.0 | 8.1 | |
| | | | | Bottom | 19 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 33.2 33.2 | 33.2 | 84.1 86.4 | 85.3 | 5.5 5.7 | 5.6 | | 6.2 6.8 | 6.5 | | 4.9 5.0 | 5.0 | |
| C2 | Sunny | Moderate | 10:19 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 97.0 102.2 | 99.6 | 6.4 6.7 | 6.6 | 6.3 | 3.3 3.3 | 3.3 | 4.5 | 5.3 5.4 | 5.4 | 5.2 |
| | | | | Middle | 17 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 86.8 91.2 | 89.0 | 5.7 6.0 | 5.9 | | 4.1 4.1 | 4.1 | | 5.2 5.2 | 5.2 | |
| | | | | Bottom | 33 | 27.4 27.3 | 27.4 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 80.9 81.6 | 81.3 | 5.3 5.4 | 5.4 | | 6.2 6.2 | 6.2 | | 4.9 4.8 | 4.9 | |
| G1 | Sunny | Moderate | 11:02 | Surface | 1 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 93.1 90.1 | 91.6 | 6.1 5.9 | 6.0 | 6.0 | 3.7 4.0 | 3.9 | 4.5 | 4.9 4.8 | 4.9 | 4.5 |
| | | | | Middle | 4 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 85.2 94.0 | 89.6 | 5.6 6.2 | 5.9 | | 4.0 4.6 | 4.3 | | 4.7 4.5 | 4.6 | |
| | | | | Bottom | 7 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 85.4 86.8 | 86.1 | 5.6 5.7 | 5.7 | | 5.3 5.2 | 5.3 | | 4.1 4.1 | 4.1 | |
| G2 | Sunny | Moderate | 10:49 | Surface | 1 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 96.9 102.0 | 99.5 | 6.4 6.7 | 6.6 | 6.3 | 3.8 3.6 | 3.7 | 4.6 | 4.5 4.4 | 4.5 | 5.3 |
| | | | | Middle | 4.5 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 86.7 91.1 | 88.9 | 5.7 6.0 | 5.9 | | 4.3 4.1 | 4.2 | | 5.7 5.7 | 5.7 | |
| | | | | Bottom | 8 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 80.9 81.7 | 81.3 | 5.3 5.4 | 5.4 | | 6.2 5.8 | 6.0 | | 5.6 5.5 | 5.6 | |
| G3 | Sunny | Moderate | 11:10 | Surface | 1 | 27.3 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.8 32.7 | 32.8 | 94.0 94.1 | 94.1 | 6.2 6.2 | 6.2 | 6.2 | 3.6 3.2 | 3.4 | 4.5 | 3.6 3.4 | 3.5 | 5.3 |
| | | | | Middle | 4 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 94.5 94.2 | 94.4 | 6.2 6.2 | 6.2 | | 4.4 4.4 | 4.4 | | 6.8 6.8 | 6.8 | |
| | | | | Bottom | 7 | 27.5 27.5 | 27.5 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 95.7 97.2 | 96.5 | 6.3 6.4 | 6.4 | | 5.6 5.9 | 5.8 | | 5.5 5.4 | 5.5 | |
| G4 | Sunny | Moderate | 11:35 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.7 32.7 | 32.7 | 80.4 76.2 | 78.3 | 5.3 5.0 | 5.2 | 5.2 | 3.4 3.5 | 3.5 | 4.6 | 4.6 4.5 | 4.6 | 4.9 |
| | | | | Middle | 4.5 | 27.3 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.7 32.8 | 32.8 | 76.5 77.8 | 77.2 | 5.1 5.1 | 5.1 | | 5.0 4.8 | 4.9 | | 5.1 4.9 | 5.0 | |
| | | | | Bottom | 8 | 27.3 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.8 32.9 | 32.9 | 77.8 72.7 | 75.3 | 5.1 4.8 | 5.0 | | 5.6 5.1 | 5.4 | | 5.2 5.1 | 5.2 | |
| M1 | Sunny | Moderate | 10:56 | Surface | 1 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 90.7 91.1 | 90.9 | 6.0 6.0 | 6.0 | 6.0 | 3.6 3.8 | 3.7 | 4.8 | 4.8 4.7 | 4.8 | 5.2 |
| | | | | Middle | 3 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 89.6 89.3 | 89.5 | 5.9 5.9 | 5.9 | | 4.8 5.0 | 4.9 | | 5.6 5.7 | 5.7 | |
| | | | | Bottom | 5 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 89.6 89.3 | 89.5 | 5.9 5.9 | 5.9 | | 6.0 5.7 | 5.9 | | 5.3 5.1 | 5.2 | |
| M2 | Sunny | Moderate | 10:41 | Surface | 1 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 89.9 90.4 | 90.2 | 5.9 6.0 | 6.0 | 6.0 | 3.6 3.8 | 3.7 | 4.7 | 5.2 5.2 | 5.2 | 4.7 |
| | | | | Middle | 6 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 88.8 89.3 | 89.1 | 5.9 5.9 | 5.9 | | 4.5 4.8 | 4.7 | | 5.1 4.8 | 5.0 | |
| | | | | Bottom | 11 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 33.1 33.0 | 33.1 | 81.1 80.4 | 80.8 | 5.3 5.3 | 5.3 | | 5.6 5.6 | 5.6 | | 4.0 3.9 | 4.0 | |
| M3 | Sunny | Moderate | 11:27 | Surface | 1 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.7 32.7 | 32.7 | 86.9 89.6 | 88.3 | 5.7 5.9 | 5.8 | 5.6 | 3.9 4.0 | 4.0 | 5.1 | 5.8 5.6 | 5.7 | 5.3 |
| | | | | Middle | 4 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.7 32.7 | 32.7 | 76.8 81.3 | 79.1 | 5.1 5.4 | 5.3 | | 4.9 5.1 | 5.0 | | 4.8 4.8 | 4.8 | |
| | | | | Bottom | 7 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.9 32.8 | 32.9 | 77.7 76.5 | 77.1 | 5.1 5.1 | 5.1 | | 6.5 6.1 | 6.3 | | 5.4 5.5 | 5.5 | |
| M4 | Sunny | Moderate | 10:31 | Surface | 1 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 99.0 97.6 | 98.3 | 6.5 6.4 | 6.5 | 6.3 | 3.8 3.6 | 3.7 | 5.0 | 4.7 4.3 | 4.5 | 5.1 |
| | | | | Middle | 5 | 27.3 27.3 | 27.3 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 91.1 91.4 | 91.3 | 6.0 6.0 | 6.0 | | 4.6 4.4 | 4.5 | | 5.4 5.5 | 5.5 | |
| | | | | Bottom | 9 | 27.3 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 88.9 88.6 | 88.8 | 5.9 5.8 | 5.9 | | 6.7 6.7 | 6.7 | | 5.3 5.2 | 5.3 | |
| M5 | Sunny | Moderate | 11:52 | Surface | 1 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.8 32.8 | 32.8 | 83.9 90.2 | 87.1 | 5.5 5.9 | 5.7 | 5.8 | 3.6 3.8 | 3.7 | 4.5 | 5.9 5.9 | 5.9 | 5.0 |
| | | | | Middle | 6 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 84.9 90.7 | 87.8 | 5.6 6.0 | 5.8 | | 4.3 5.0 | 4.7 | | 4.2 4.2 | 4.2 | |
| | | | | Bottom | 11 | 27.4 27.4 | 27.4 | 8.3 8.3 | 8.3 | 33.1 33.1 | 33.1 | 87.2 81.9 | 84.6 | 5.7 5.4 | 5.6 | | 5.1 5.2 | 5.2 | | 4.9 4.7 | 4.8 | |
| M6 | Sunny | Moderate | 11:44 | Surface | - | - | - | - | - | - | - | - | - | - | - | 6.3 | - | - | 3.1 | - | - | 5.0 |
| | | | | Middle | 2.2 | 27.6 27.6 | 27.6 | 8.3 8.3 | 8.3 | 31.1 31.1 | 31.1 | 95.3 94.8 | 95.1 | 6.3 6.3 | 6.3 | | 3.2 3.0 | 3.1 | | 5.0 5.0 | 5.0 | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 18 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 7.4 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 8.1 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.5 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.0 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.5 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.0 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.9 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.4 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 18 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|------------|-------------------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 17:46 | Surface | 1 | 27.8 27.9 | 27.9 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 95.0 95.2 | 95.1 | 6.2 6.2 | 6.2 | 6.2 | 3.4 3.4 | 3.4 | 4.5 | 3.7 3.6 | 3.7 | 4.6 |
| | | | | Middle | 9 | 27.7 27.8 | 27.8 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 93.6 93.9 | 93.8 | 6.1 6.1 | 6.1 | 4.7 4.6 | 4.7 | 5.6 5.6 | | 5.6 | | |
| | | | | Bottom | 17 | 27.6 27.6 | 27.6 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 92.5 92.6 | 92.6 | 6.1 6.1 | 6.1 | 5.4 5.5 | 5.5 | 4.6 4.6 | | 4.6 | | |
| C2 | Sunny | Moderate | 16:17 | Surface | 1 | 27.7 27.8 | 27.8 | 8.3 8.3 | 8.3 | 32.9 33.0 | 33.0 | 94.6 94.6 | 94.6 | 6.2 6.2 | 6.2 | 3.4 3.4 | 3.4 | 4.5 | 4.3 4.1 | 4.2 | 4.5 | |
| | | | | Middle | 17 | 27.7 27.7 | 27.7 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 93.6 93.7 | 93.7 | 6.1 6.1 | 6.1 | 4.6 4.5 | 4.6 | | 4.2 4.2 | 4.2 | | |
| | | | | Bottom | 33 | 27.6 27.6 | 27.6 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 92.5 92.8 | 92.8 | 6.1 6.1 | 6.1 | 5.4 5.8 | 5.6 | | 5.1 4.8 | 5.0 | | |
| G1 | Sunny | Moderate | 16:51 | Surface | 1 | 27.8 27.8 | 27.8 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 94.6 94.8 | 94.7 | 6.2 6.2 | 6.2 | 3.4 3.4 | 3.4 | 4.5 | 3.1 3.2 | 3.2 | 4.4 | |
| | | | | Middle | 4 | 27.7 27.7 | 27.7 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 93.8 93.8 | 93.8 | 6.2 6.2 | 6.2 | 4.7 4.6 | 4.7 | | 5.9 5.9 | 5.9 | | |
| | | | | Bottom | 7 | 27.6 27.7 | 27.7 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 93.6 94.0 | 93.8 | 6.1 6.2 | 6.2 | 5.2 5.3 | 5.3 | | 4.0 3.9 | 4.0 | | |
| G2 | Sunny | Moderate | 16:45 | Surface | 1 | 27.7 27.1 | 27.4 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 95.0 92.8 | 93.9 | 6.2 6.1 | 6.2 | 3.4 3.7 | 3.6 | 4.5 | 3.9 3.7 | 3.8 | 4.5 | |
| | | | | Middle | 4.5 | 27.7 27.1 | 27.4 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 94.3 92.0 | 93.2 | 6.2 6.1 | 6.2 | 4.8 4.5 | 4.7 | | 5.4 5.6 | 5.5 | | |
| | | | | Bottom | 8 | 27.6 27.0 | 27.3 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 93.5 93.1 | 93.3 | 6.1 6.2 | 6.2 | 5.4 4.9 | 5.2 | | 4.2 4.2 | 4.2 | | |
| G3 | Sunny | Moderate | 16:58 | Surface | 1 | 27.8 27.8 | 27.8 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 94.8 94.8 | 94.8 | 6.2 6.2 | 6.2 | 3.4 3.3 | 3.4 | 4.4 | 3.3 3.2 | 3.3 | 5.3 | |
| | | | | Middle | 4 | 27.7 27.7 | 27.7 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 93.7 93.8 | 93.8 | 6.1 6.2 | 6.2 | 4.6 4.5 | 4.6 | | 7.3 7.3 | 7.3 | | |
| | | | | Bottom | 7 | 27.7 27.7 | 27.7 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 93.8 93.8 | 93.8 | 6.2 6.2 | 6.2 | 5.2 5.1 | 5.2 | | 5.3 5.3 | 5.3 | | |
| G4 | Sunny | Moderate | 17:18 | Surface | 1 | 27.8 27.8 | 27.8 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 95.1 94.7 | 94.9 | 6.2 6.2 | 6.2 | 3.7 3.4 | 3.6 | 4.7 | 4.3 4.4 | 4.4 | 4.9 | |
| | | | | Middle | 4.5 | 27.7 27.7 | 27.7 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 94.1 93.8 | 94.0 | 6.2 6.1 | 6.2 | 4.6 4.6 | 4.6 | | 5.7 5.4 | 5.6 | | |
| | | | | Bottom | 8 | 27.6 27.6 | 27.6 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 92.9 93.2 | 93.1 | 6.1 6.1 | 6.1 | 5.6 5.9 | 5.8 | | 4.7 4.6 | 4.7 | | |
| M1 | Sunny | Moderate | 16:43 | Surface | 1 | 27.7 27.7 | 27.7 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 95.0 94.5 | 94.8 | 6.2 6.2 | 6.2 | 3.4 3.3 | 3.4 | 4.5 | 3.5 3.3 | 3.4 | 4.6 | |
| | | | | Middle | 3 | 27.7 27.7 | 27.7 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 94.2 94.0 | 94.1 | 6.2 6.2 | 6.2 | 4.7 4.6 | 4.7 | | 6.9 6.8 | 6.9 | | |
| | | | | Bottom | 5 | 27.6 27.6 | 27.6 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 93.6 93.5 | 93.6 | 6.1 6.1 | 6.1 | 5.3 5.3 | 5.3 | | 3.5 3.4 | 3.5 | | |
| M2 | Sunny | Moderate | 16:35 | Surface | 1 | 27.7 27.8 | 27.8 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 94.7 94.7 | 94.7 | 6.2 6.2 | 6.2 | 3.3 3.4 | 3.4 | 4.6 | 3.8 3.8 | 3.8 | 5.7 | |
| | | | | Middle | 6 | 27.6 27.7 | 27.7 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 93.5 94.0 | 93.8 | 6.1 6.2 | 6.2 | 4.6 4.7 | 4.7 | | 8.2 8.1 | 8.2 | | |
| | | | | Bottom | 11 | 27.6 27.6 | 27.6 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 92.9 92.9 | 92.9 | 6.1 6.1 | 6.1 | 5.6 5.9 | 5.8 | | 5.2 5.2 | 5.2 | | |
| M3 | Sunny | Moderate | 17:10 | Surface | 1 | 27.0 27.1 | 27.1 | 8.4 8.4 | 8.4 | 32.3 32.3 | 32.3 | 84.4 83.8 | 84.1 | 5.6 5.6 | 5.6 | 3.8 3.7 | 3.8 | 4.5 | 3.3 3.5 | 3.4 | 4.7 | |
| | | | | Middle | 4 | 27.5 27.4 | 27.5 | 8.3 8.3 | 8.3 | 32.7 32.8 | 32.8 | 78.3 76.8 | 77.6 | 5.2 5.1 | 5.2 | 4.0 4.2 | 4.1 | | 5.5 5.6 | 5.6 | | |
| | | | | Bottom | 7 | 28.0 27.9 | 28.0 | 8.3 8.3 | 8.3 | 33.2 33.4 | 33.3 | 81.9 78.6 | 80.3 | 5.3 5.1 | 5.2 | 5.4 5.7 | 5.6 | | 5.1 5.1 | 5.1 | | |
| M4 | Sunny | Moderate | 16:27 | Surface | 1 | 27.7 27.7 | 27.7 | 8.3 8.3 | 8.3 | 33.0 32.9 | 33.0 | 94.6 94.7 | 94.7 | 6.2 6.2 | 6.2 | 3.4 3.2 | 3.3 | 4.4 | 4.0 3.8 | 3.9 | 4.9 | |
| | | | | Middle | 5 | 27.7 27.7 | 27.7 | 8.3 8.3 | 8.3 | 33.0 32.9 | 33.0 | 94.0 94.0 | 94.0 | 6.2 6.2 | 6.2 | 4.4 4.5 | 4.5 | | 5.5 5.5 | 5.5 | | |
| | | | | Bottom | 9 | 27.6 27.6 | 27.6 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 93.2 93.2 | 93.2 | 6.1 6.1 | 6.1 | 5.4 5.3 | 5.4 | | 5.2 5.2 | 5.2 | | |
| M5 | Sunny | Moderate | 17:36 | Surface | 1 | 27.8 27.9 | 27.9 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 94.9 95.0 | 95.0 | 6.2 6.2 | 6.2 | 3.4 3.4 | 3.4 | 4.5 | 3.2 3.3 | 3.3 | 4.3 | |
| | | | | Middle | 6 | 27.7 27.6 | 27.7 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 93.5 93.3 | 93.4 | 6.1 6.1 | 6.1 | 4.8 4.6 | 4.7 | | 4.5 4.4 | 4.5 | | |
| | | | | Bottom | 11 | 27.6 27.6 | 27.6 | 8.3 8.3 | 8.3 | 33.0 33.0 | 33.0 | 92.9 92.7 | 92.8 | 6.1 6.1 | 6.1 | 5.6 5.4 | 5.5 | | 5.2 5.2 | 5.2 | | |
| M6 | Sunny | Moderate | 17:28 | Surface | - | - | - | - | - | - | - | - | - | - | - | - | - | 3.4 | - | - | 5.7 | |
| | | | | Middle | 2.2 | 27.8 27.8 | 27.8 | 8.3 8.3 | 8.3 | 32.9 32.9 | 32.9 | 94.7 94.6 | 94.7 | 6.2 6.2 | 6.2 | 3.4 3.4 | 3.4 | | 5.7 5.7 | 5.7 | | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | - | - | | - | - | | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 18 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 6.6 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 7.2 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 4.4 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 4.8 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 4.4 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 4.8 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.5 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.0 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 20 October 2017**

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 13:13 | Surface | 1 | 28.3 28.5 | 28.4 | 8.1 8.1 | 8.1 | 30.8 30.6 | 30.7 | 77.3 78.5 | 77.9 | 5.1 5.1 | 5.1 | 5.2 | 1.9 1.8 | 1.9 | 2.7 | 5.1 5.2 | 5.2 | 5.9 |
| | | | | Middle | 9.5 | 28.3 28.2 | 28.3 | 8.2 8.2 | 8.2 | 31.1 31.0 | 31.1 | 80.4 77.1 | 78.8 | 5.3 5.1 | 5.2 | 5.3 | 1.7 | 1.7 | | 6.1 6.0 | 6.1 | |
| | | | | Bottom | 18 | 28.4 28.3 | 28.4 | 8.2 8.2 | 8.2 | 31.4 31.3 | 31.4 | 81.7 81.3 | 81.5 | 5.3 5.3 | 5.3 | 5.3 | 4.9 4.3 | 4.6 | | 6.3 6.4 | 6.4 | |
| C2 | Sunny | Moderate | 11:26 | Surface | 1 | 28.2 28.2 | 28.2 | 8.1 8.1 | 8.1 | 30.6 30.6 | 30.6 | 74.9 74.4 | 74.7 | 4.9 4.9 | 4.9 | 5.0 | 2.0 2.1 | 2.1 | 3.7 | 5.7 5.5 | 5.6 | 5.8 |
| | | | | Middle | 17 | 28.2 28.2 | 28.2 | 8.1 8.1 | 8.1 | 31.0 31.0 | 31.0 | 77.5 77.7 | 77.6 | 5.1 5.1 | 5.1 | 5.1 | 2.3 2.5 | 2.4 | | 5.8 5.9 | 5.9 | |
| | | | | Bottom | 33 | 28.3 28.3 | 28.3 | 8.2 8.2 | 8.2 | 31.2 31.2 | 31.2 | 80.9 80.4 | 80.7 | 5.3 5.3 | 5.3 | 5.3 | 6.7 6.6 | 6.7 | | 5.7 5.9 | 5.8 | |
| G1 | Sunny | Moderate | 12:16 | Surface | 1 | 28.2 28.3 | 28.3 | 8.1 8.1 | 8.1 | 30.9 30.8 | 30.9 | 76.0 76.3 | 76.2 | 5.0 5.0 | 5.0 | 5.0 | 1.6 1.5 | 1.6 | 3.1 | 5.1 5.2 | 5.2 | 6.5 |
| | | | | Middle | 4 | 28.2 28.2 | 28.2 | 8.1 8.1 | 8.1 | 30.9 30.9 | 30.9 | 76.0 76.6 | 76.3 | 5.0 5.0 | 5.0 | 5.0 | 2.7 3.0 | 2.9 | | 8.6 8.4 | 8.5 | |
| | | | | Bottom | 7 | 28.1 28.1 | 28.1 | 8.1 8.1 | 8.1 | 31.0 31.0 | 31.0 | 74.3 73.7 | 74.0 | 4.9 4.8 | 4.9 | 4.9 | 4.6 5.2 | 4.9 | | 5.7 5.6 | 5.7 | |
| G2 | Sunny | Moderate | 11:55 | Surface | 1 | 28.3 28.2 | 28.3 | 8.1 8.1 | 8.1 | 30.8 30.9 | 30.9 | 76.6 75.7 | 76.2 | 5.0 5.0 | 5.0 | 5.0 | 1.9 1.8 | 1.9 | 3.9 | 5.6 5.5 | 5.6 | 7.1 |
| | | | | Middle | 4.5 | 28.2 28.2 | 28.2 | 8.2 8.2 | 8.2 | 31.1 31.0 | 31.1 | 74.8 75.1 | 75.0 | 4.9 4.9 | 4.9 | 4.9 | 4.7 4.7 | 4.7 | | 8.9 8.9 | 8.9 | |
| | | | | Bottom | 8 | 28.2 28.2 | 28.2 | 8.2 8.2 | 8.2 | 31.1 31.0 | 31.1 | 74.8 76.0 | 75.4 | 4.9 5.0 | 5.0 | 5.0 | 5.0 5.2 | 5.1 | | 6.7 6.8 | 6.8 | |
| G3 | Sunny | Moderate | 12:26 | Surface | 1 | 28.3 28.3 | 28.3 | 8.1 8.1 | 8.1 | 30.8 29.3 | 30.1 | 77.7 73.1 | 75.4 | 5.1 4.8 | 5.0 | 5.1 | 2.0 1.9 | 2.0 | 2.6 | 4.5 4.3 | 4.4 | 4.9 |
| | | | | Middle | 4 | 28.2 28.2 | 28.2 | 8.2 8.1 | 8.2 | 30.9 29.4 | 30.2 | 78.5 73.9 | 76.2 | 5.2 4.9 | 5.1 | 5.1 | 1.8 1.7 | 1.8 | | 4.2 4.2 | 4.2 | |
| | | | | Bottom | 7 | 28.1 28.1 | 28.1 | 8.1 8.2 | 8.2 | 31.0 29.5 | 30.3 | 75.9 71.4 | 73.7 | 5.0 4.7 | 4.9 | 4.9 | 4.0 3.8 | 3.9 | | 6.2 6.2 | 6.2 | |
| G4 | Sunny | Moderate | 12:41 | Surface | 1 | 28.3 28.3 | 28.3 | 8.1 8.1 | 8.1 | 30.6 30.6 | 30.6 | 77.5 76.7 | 77.1 | 5.1 5.0 | 5.1 | 5.1 | 2.0 2.1 | 2.1 | 2.0 | 4.5 4.3 | 4.4 | 5.1 |
| | | | | Middle | 4.5 | 28.2 28.2 | 28.2 | 8.1 8.1 | 8.1 | 30.7 30.8 | 30.8 | 75.3 75.4 | 75.4 | 5.0 5.0 | 5.0 | 5.0 | 2.2 2.0 | 2.1 | | 5.9 5.9 | 5.9 | |
| | | | | Bottom | 8 | 28.3 28.2 | 28.3 | 8.2 8.2 | 8.2 | 31.0 31.0 | 31.0 | 79.3 77.4 | 78.4 | 5.2 5.1 | 5.2 | 5.2 | 1.6 2.0 | 1.8 | | 4.9 4.9 | 4.9 | |
| M1 | Sunny | Moderate | 12:05 | Surface | 1 | 28.2 28.2 | 28.2 | 8.1 8.1 | 8.1 | 31.0 30.8 | 30.9 | 75.2 75.8 | 75.5 | 4.9 5.0 | 5.0 | 5.0 | 1.9 1.9 | 1.9 | 3.3 | 4.0 4.0 | 4.0 | 4.2 |
| | | | | Middle | 3 | 28.2 28.2 | 28.2 | 8.2 8.1 | 8.2 | 31.0 31.0 | 31.0 | 75.7 75.2 | 75.5 | 5.0 4.9 | 5.0 | 5.0 | 3.7 3.8 | 3.8 | | 4.2 4.1 | 4.2 | |
| | | | | Bottom | 5 | 28.2 28.2 | 28.2 | 8.2 8.1 | 8.2 | 31.0 31.0 | 31.0 | 75.5 76.1 | 75.8 | 5.0 5.0 | 5.0 | 5.0 | 4.1 4.1 | 4.1 | | 4.5 4.5 | 4.5 | |
| M2 | Sunny | Moderate | 11:45 | Surface | 1 | 28.3 28.3 | 28.3 | 8.1 8.1 | 8.1 | 30.7 30.7 | 30.7 | 78.6 76.8 | 77.7 | 5.2 5.0 | 5.1 | 5.1 | 1.8 1.7 | 1.8 | 4.2 | 4.8 4.6 | 4.7 | 4.1 |
| | | | | Middle | 6 | 28.3 28.2 | 28.3 | 8.2 8.2 | 8.2 | 31.1 31.1 | 31.1 | 77.7 75.0 | 76.4 | 5.1 4.9 | 5.0 | 5.0 | 5.7 5.3 | 5.5 | | 3.8 3.7 | 3.8 | |
| | | | | Bottom | 11 | 28.3 28.2 | 28.3 | 8.2 8.2 | 8.2 | 31.2 31.1 | 31.2 | 74.4 73.8 | 74.1 | 4.9 4.8 | 4.9 | 4.9 | 5.1 5.3 | 5.2 | | 3.8 3.8 | 3.8 | |
| M3 | Sunny | Moderate | 12:32 | Surface | 1 | 28.1 28.2 | 28.2 | 8.2 8.2 | 8.2 | 30.1 30.1 | 30.1 | 82.4 81.7 | 82.1 | 5.4 5.4 | 5.4 | 5.2 | 1.9 1.8 | 1.9 | 3.2 | 5.9 5.8 | 5.9 | 5.2 |
| | | | | Middle | 4 | 27.6 27.6 | 27.6 | 8.1 8.1 | 8.1 | 30.5 30.6 | 30.6 | 75.2 73.8 | 74.5 | 5.0 4.9 | 5.0 | 5.0 | 3.2 3.2 | 3.2 | | 5.5 5.4 | 5.5 | |
| | | | | Bottom | 7 | 27.1 27.0 | 27.1 | 8.2 8.2 | 8.2 | 31.0 31.2 | 31.1 | 77.4 74.3 | 75.9 | 5.2 5.0 | 5.1 | 5.1 | 4.6 4.6 | 4.6 | | 4.2 4.1 | 4.2 | |
| M4 | Sunny | Moderate | 11:36 | Surface | 1 | 28.2 28.2 | 28.2 | 8.1 8.1 | 8.1 | 30.9 31.0 | 31.0 | 76.6 76.2 | 76.4 | 5.0 5.0 | 5.0 | 5.0 | 2.4 3.0 | 2.7 | 3.1 | 5.5 5.5 | 5.5 | 5.9 |
| | | | | Middle | 5 | 28.2 28.2 | 28.2 | 8.2 8.1 | 8.2 | 31.0 31.0 | 31.0 | 76.0 75.8 | 75.9 | 5.0 5.0 | 5.0 | 5.0 | 3.4 3.5 | 3.5 | | 5.7 6.5 | 5.6 | |
| | | | | Bottom | 9 | 28.2 28.2 | 28.2 | 8.1 8.1 | 8.1 | 31.0 31.0 | 31.0 | 76.1 75.8 | 76.0 | 5.0 5.0 | 5.0 | 5.0 | 3.2 3.2 | 3.2 | | 5.3 6.6 | 6.5 | |
| M5 | Sunny | Moderate | 13:00 | Surface | 1 | 28.4 28.4 | 28.4 | 8.1 8.1 | 8.1 | 30.6 30.6 | 30.6 | 77.3 77.1 | 77.2 | 5.1 5.1 | 5.1 | 5.1 | 2.0 1.8 | 1.9 | 2.7 | 4.0 4.1 | 4.1 | 4.5 |
| | | | | Middle | 6 | 28.2 28.2 | 28.2 | 8.2 8.2 | 8.2 | 30.9 30.9 | 30.9 | 77.2 76.6 | 76.9 | 5.1 5.0 | 5.1 | 5.1 | 1.7 1.7 | 1.7 | | 3.2 3.1 | 3.2 | |
| | | | | Bottom | 11 | 28.3 28.3 | 28.3 | 8.2 8.2 | 8.2 | 31.3 31.4 | 31.4 | 82.0 82.0 | 82.0 | 5.4 5.4 | 5.4 | 5.4 | 4.5 4.4 | 4.5 | | 6.0 6.1 | 6.1 | |
| M6 | Sunny | Moderate | 12:52 | Surface | - | - | - | - | - | - | - | - | - | - | - | - | - | - | 2.0 | - | - | 6.7 |
| | | | | Middle | 2.2 | 28.3 28.3 | 28.3 | 8.1 8.1 | 8.1 | 30.6 30.6 | 30.6 | 78.1 78.3 | 78.2 | 5.1 5.1 | 5.1 | 5.1 | 2.0 2.0 | 2.0 | | 6.7 6.7 | 6.7 | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | - | - | - | | - | - | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 20 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 8.0 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 8.7 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.7 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.3 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.7 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.3 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.0 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.5 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 20 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|---------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 18:46 | Surface | 1 | 28.9 29.4 | 29.2 | 8.2 8.2 | 8.2 | 28.1 26.7 | 27.4 | 84.1 100.1 | 92.1 | 5.6 6.6 | 6.1 | 5.2 | 1.6 1.6 | 1.6 | 3.5 | 5.8 5.7 | 5.8 | 4.8 |
| | | | | Middle | 9.5 | 26.8 27.4 | 27.1 | 8.2 8.2 | 8.2 | 29.3 27.8 | 28.6 | 65.4 62.3 | 63.9 | 4.4 4.2 | 4.3 | | 2.2 2.2 | 2.2 | | 3.4 3.4 | 3.5 | |
| | | | | Bottom | 18 | 24.9 25.6 | 25.3 | 8.1 8.1 | 8.1 | 33.2 31.6 | 32.4 | 63.4 61.7 | 62.6 | 4.4 4.2 | 4.3 | | 6.7 6.6 | 6.7 | | 5.0 5.0 | 5.0 | |
| C2 | Sunny | Moderate | 17:06 | Surface | 1 | 28.7 28.8 | 28.8 | 8.2 8.2 | 8.2 | 27.7 27.6 | 27.7 | 85.9 85.4 | 85.7 | 5.7 5.7 | 5.7 | 5.4 | 1.8 1.8 | 1.8 | 3.2 | 2.8 2.8 | 2.8 | 4.5 |
| | | | | Middle | 17 | 26.5 26.5 | 26.5 | 8.1 8.1 | 8.1 | 29.7 29.7 | 29.7 | 73.7 75.0 | 74.4 | 5.0 5.1 | 5.1 | | 3.0 2.7 | 2.9 | | 6.3 6.5 | 6.4 | |
| | | | | Bottom | 33 | 26.1 26.2 | 26.2 | 8.1 8.1 | 8.1 | 30.8 30.6 | 30.7 | 65.6 66.6 | 66.1 | 4.5 4.5 | 4.5 | | 5.0 5.0 | 5.0 | | 4.2 4.5 | 4.4 | |
| G1 | Sunny | Moderate | 18:01 | Surface | 1 | 27.9 27.9 | 27.9 | 8.2 8.2 | 8.2 | 28.5 28.5 | 28.5 | 91.0 91.0 | 91.0 | 6.1 6.1 | 6.1 | 6.0 | 1.9 1.9 | 1.9 | 2.3 | 4.2 4.3 | 4.3 | 4.5 |
| | | | | Middle | 3 | 27.9 27.7 | 27.8 | 8.2 8.2 | 8.2 | 28.6 28.7 | 28.7 | 89.3 85.8 | 87.6 | 6.0 5.8 | 5.9 | | 2.0 2.4 | 2.2 | | 5.7 5.7 | 5.7 | |
| | | | | Bottom | 5 | 27.6 27.6 | 27.6 | 8.2 8.2 | 8.2 | 28.8 28.8 | 28.8 | 81.0 79.8 | 80.4 | 5.4 5.4 | 5.4 | | 3.0 2.7 | 2.9 | | 3.5 3.7 | 3.6 | |
| G2 | Sunny | Moderate | 17:38 | Surface | 1 | 28.0 28.0 | 28.0 | 8.2 8.2 | 8.2 | 28.1 28.1 | 28.1 | 75.9 76.3 | 76.1 | 5.1 5.1 | 5.1 | 5.4 | 2.4 2.2 | 2.3 | 2.7 | 3.2 3.3 | 3.3 | 4.4 |
| | | | | Middle | 4 | 27.7 27.7 | 27.7 | 8.2 8.2 | 8.2 | 28.7 28.7 | 28.7 | 84.4 84.2 | 84.3 | 5.7 5.7 | 5.7 | | 1.9 1.8 | 1.9 | | 6.1 6.3 | 6.2 | |
| | | | | Bottom | 7 | 27.3 27.4 | 27.4 | 8.1 8.1 | 8.1 | 29.2 29.1 | 29.2 | 71.6 77.3 | 74.5 | 4.8 5.2 | 5.0 | | 4.2 3.5 | 3.9 | | 3.7 3.8 | 3.8 | |
| G3 | Sunny | Moderate | 18:08 | Surface | 1 | 28.2 28.1 | 28.2 | 8.2 8.1 | 8.2 | 27.6 27.8 | 27.7 | 83.5 95.3 | 89.4 | 5.6 6.4 | 6.0 | 5.7 | 2.3 2.1 | 2.2 | 3.6 | 4.3 4.5 | 4.4 | 4.7 |
| | | | | Middle | 3.5 | 27.5 27.5 | 27.5 | 8.2 8.2 | 8.2 | 28.8 28.8 | 28.8 | 78.7 78.1 | 78.4 | 5.3 5.3 | 5.3 | | 2.6 2.5 | 2.6 | | 6.4 6.4 | 6.4 | |
| | | | | Bottom | 6 | 27.1 27.1 | 27.1 | 8.2 8.2 | 8.2 | 29.2 29.2 | 29.2 | 63.8 64.7 | 64.3 | 4.3 4.4 | 4.4 | | 5.9 5.8 | 5.9 | | 3.2 3.2 | 3.2 | |
| G4 | Sunny | Moderate | 18:24 | Surface | 1 | 28.0 28.0 | 28.0 | 8.2 8.2 | 8.2 | 28.5 28.4 | 28.5 | 95.3 95.2 | 95.3 | 6.4 6.4 | 6.4 | 6.2 | 2.8 3.0 | 2.9 | 2.6 | 5.7 5.4 | 5.6 | 6.1 |
| | | | | Middle | 4 | 27.8 27.9 | 27.9 | 8.2 8.2 | 8.2 | 28.6 28.6 | 28.6 | 88.9 89.6 | 89.3 | 6.0 6.0 | 6.0 | | 1.9 1.8 | 1.9 | | 7.0 7.0 | 7.0 | |
| | | | | Bottom | 7 | 27.6 27.6 | 27.6 | 8.2 8.2 | 8.2 | 28.8 28.8 | 28.8 | 79.7 79.8 | 79.8 | 5.4 5.4 | 5.4 | | 3.1 3.1 | 3.1 | | 5.8 5.8 | 5.8 | |
| M1 | Sunny | Moderate | 17:50 | Surface | 1 | 27.7 27.8 | 27.8 | 8.2 8.2 | 8.2 | 28.5 28.4 | 28.5 | 85.5 84.9 | 85.2 | 5.7 5.7 | 5.7 | 5.7 | 2.7 2.6 | 2.7 | 2.8 | 4.9 5.0 | 5.0 | 5.7 |
| | | | | Middle | 3 | 27.7 27.7 | 27.7 | 8.2 8.2 | 8.2 | 28.6 28.6 | 28.6 | 85.1 85.1 | 85.1 | 5.7 5.7 | 5.7 | | 2.3 2.4 | 2.4 | | 6.3 6.3 | 6.3 | |
| | | | | Bottom | 5 | 27.5 27.6 | 27.6 | 8.1 8.2 | 8.2 | 28.9 28.7 | 28.8 | 75.4 87.4 | 78.7 | 5.1 5.5 | 5.3 | | 3.3 3.3 | 3.3 | | 5.8 6.0 | 5.9 | |
| M2 | Sunny | Moderate | 17:27 | Surface | 1 | 28.2 28.4 | 28.3 | 8.2 8.2 | 8.2 | 28.0 27.9 | 28.0 | 84.5 87.1 | 85.8 | 5.6 5.8 | 5.7 | 5.6 | 2.0 1.9 | 2.0 | 2.0 | 4.4 4.4 | 4.4 | 4.4 |
| | | | | Middle | 5.5 | 27.6 27.5 | 27.6 | 8.2 8.2 | 8.2 | 28.8 28.9 | 28.9 | 80.7 80.1 | 80.4 | 5.4 5.4 | 5.4 | | 2.1 2.2 | 2.2 | | 5.2 5.1 | 5.2 | |
| | | | | Bottom | 10 | 28.4 27.2 | 27.8 | 8.1 8.1 | 8.1 | 27.6 29.3 | 28.5 | 87.2 87.4 | 87.3 | 5.8 5.9 | 5.9 | | 1.9 1.9 | 1.9 | | 3.5 3.5 | 3.5 | |
| M3 | Sunny | Moderate | 18:14 | Surface | 1 | 28.1 28.0 | 28.1 | 8.2 8.2 | 8.2 | 27.8 27.9 | 27.9 | 93.5 93.6 | 93.6 | 6.3 6.3 | 6.3 | 5.4 | 2.2 2.3 | 2.3 | 3.9 | 4.4 4.3 | 4.4 | 4.2 |
| | | | | Middle | 3.5 | 27.4 27.4 | 27.4 | 8.2 8.2 | 8.2 | 28.7 28.7 | 28.7 | 64.8 68.0 | 66.4 | 4.4 4.6 | 4.5 | | 4.2 3.8 | 4.0 | | 4.2 4.2 | 4.2 | |
| | | | | Bottom | 6 | 27.2 27.2 | 27.2 | 8.2 8.2 | 8.2 | 29.1 29.0 | 29.1 | 63.4 64.2 | 63.8 | 4.3 4.3 | 4.3 | | 5.8 5.2 | 5.5 | | 4.0 4.0 | 4.0 | |
| M4 | Sunny | Moderate | 17:17 | Surface | 1 | 28.9 28.9 | 28.9 | 8.2 8.2 | 8.2 | 27.4 27.4 | 27.4 | 92.2 91.8 | 92.0 | 6.1 6.1 | 6.1 | 5.7 | 2.0 1.9 | 2.0 | 2.0 | 3.6 3.6 | 3.6 | 3.7 |
| | | | | Middle | 4.5 | 28.1 28.0 | 28.1 | 8.2 8.2 | 8.2 | 28.1 28.1 | 28.1 | 78.8 79.8 | 79.3 | 5.3 5.3 | 5.3 | | 1.9 1.9 | 1.9 | | 4.2 4.0 | 4.1 | |
| | | | | Bottom | 8 | 28.0 27.9 | 28.0 | 8.1 8.1 | 8.1 | 28.4 28.2 | 28.3 | 86.3 92.8 | 89.6 | 5.8 6.2 | 6.0 | | 2.1 2.0 | 2.1 | | 3.3 3.2 | 3.3 | |
| M5 | Sunny | Moderate | 18:36 | Surface | 1 | 27.6 27.6 | 27.6 | 8.2 8.2 | 8.2 | 28.8 28.8 | 28.8 | 82.8 82.9 | 82.9 | 5.6 5.6 | 5.6 | 5.4 | 2.8 2.7 | 2.8 | 3.2 | 4.8 4.9 | 4.9 | 4.2 |
| | | | | Middle | 5.5 | 27.4 27.3 | 27.4 | 8.1 8.1 | 8.1 | 29.1 29.3 | 29.2 | 79.5 75.9 | 77.7 | 5.3 5.1 | 5.2 | | 3.0 2.7 | 2.9 | | 3.7 3.7 | 3.7 | |
| | | | | Bottom | 10 | 27.2 27.2 | 27.2 | 8.1 8.1 | 8.1 | 29.4 29.3 | 29.4 | 73.5 74.2 | 73.9 | 5.0 5.0 | 5.0 | | 3.9 3.9 | 3.9 | | 4.0 4.0 | 4.0 | |
| M6 | Sunny | Moderate | 18:32 | Surface | - | - | - | - | - | - | - | - | - | - | 6.2 | - | - | 2.2 | - | - | 6.3 | |
| | | | | Middle | 2.1 | 27.9 27.9 | 27.9 | 8.2 8.2 | 8.2 | 28.5 28.5 | 28.5 | 92.0 92.3 | 92.2 | 6.2 6.2 | | 6.2 | 2.2 2.2 | | 2.2 | 6.3 6.2 | | 6.3 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 20 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 8.0 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 8.7 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.0 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.5 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.0 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.5 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.0 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.5 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 23 October 2017**

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|------------|-------------------------|-------------|--------------|-----|------|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | | |
| C1 | Sunny | Moderate | 15:33 | Surface | 1 | 27.0 27.1 | 27.1 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 96.8 96.6 | 96.7 | 6.4 6.4 | 6.4 | 6.4 | 3.3 | 3.1 3.2 | 3.2 | 5.0 | 3.9 3.9 | 3.9 | 4.1 |
| | | | | Middle | 9 | 27.0 27.0 | 27.0 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 95.6 95.4 | 95.5 | 6.3 6.3 | 6.3 | 6.3 | | 2.8 2.8 | 2.8 | | 4.4 4.4 | 4.4 | |
| | | | | Bottom | 17 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 92.7 93.6 | 93.2 | 6.2 6.2 | 6.2 | 6.2 | | 3.9 3.7 | 3.8 | | 5.1 5.0 | 5.1 | |
| C2 | Sunny | Moderate | 14:16 | Surface | 1 | 27.0 27.0 | 27.0 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 91.9 91.9 | 91.9 | 6.1 6.1 | 6.1 | 6.1 | 4.2 4.0 | 4.1 | 5.0 | 4.3 5.3 | 4.8 | 4.9 | |
| | | | | Middle | 17 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.0 91.0 | 91.0 | 6.0 6.0 | 6.0 | | 6.0 | 4.0 3.9 | | 4.0 | 4.6 4.4 | | 4.5 |
| | | | | Bottom | 33 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.5 91.5 | 91.5 | 6.1 6.1 | 6.1 | | 6.1 | 7.0 7.0 | | 7.0 | 5.5 5.5 | | 5.5 |
| G1 | Sunny | Moderate | 14:53 | Surface | 1 | 26.9 26.9 | 26.9 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 95.5 95.2 | 95.4 | 6.3 6.3 | 6.3 | 6.2 | 3.4 3.3 | 3.4 | 5.4 | 4.2 4.4 | 4.3 | 5.0 | |
| | | | | Middle | 4 | 26.6 26.7 | 26.7 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 90.4 91.3 | 90.9 | 6.0 6.1 | 6.1 | | 6.1 | 4.8 4.7 | | 4.8 | 6.2 6.1 | | 6.2 |
| | | | | Bottom | 7 | 26.4 26.5 | 26.5 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 87.4 87.7 | 87.6 | 5.8 5.8 | 5.8 | | 5.8 | 8.1 8.1 | | 8.1 | 4.4 4.6 | | 4.5 |
| G2 | Sunny | Moderate | 14:40 | Surface | 1 | 26.9 26.8 | 26.9 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 94.0 93.5 | 93.8 | 6.2 6.2 | 6.2 | 6.1 | 4.4 4.2 | 4.3 | 5.2 | 4.4 4.5 | 4.5 | 6.5 | |
| | | | | Middle | 5 | 26.6 26.6 | 26.6 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 89.9 89.9 | 89.9 | 6.0 6.0 | 6.0 | | 6.0 | 5.9 5.9 | | 5.9 | 10.6 10.6 | | 10.6 |
| | | | | Bottom | 9 | 26.6 26.6 | 26.6 | 8.4 8.4 | 8.4 | 33.7 33.7 | 33.7 | 89.9 89.9 | 89.9 | 6.0 6.0 | 6.0 | | 6.0 | 5.5 5.1 | | 5.3 | 4.4 4.4 | | 4.4 |
| G3 | Sunny | Moderate | 14:59 | Surface | 1 | 26.7 26.7 | 26.7 | 8.4 8.4 | 8.4 | 33.5 33.5 | 33.5 | 91.6 91.1 | 91.4 | 6.1 6.1 | 6.1 | 6.0 | 3.5 3.5 | 3.5 | 4.0 | 4.4 4.4 | 4.4 | 4.9 | |
| | | | | Middle | 4 | 26.7 26.7 | 26.7 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 87.6 88.5 | 88.1 | 5.8 5.9 | 5.9 | | 5.9 | 3.8 3.6 | | 3.7 | 5.8 5.8 | | 5.8 |
| | | | | Bottom | 7 | 26.6 26.6 | 26.6 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 88.9 88.8 | 88.9 | 5.9 5.9 | 5.9 | | 5.9 | 4.8 4.7 | | 4.8 | 4.5 4.5 | | 4.5 |
| G4 | Sunny | Moderate | 15:13 | Surface | 1 | 27.1 27.1 | 27.1 | 8.4 8.4 | 8.4 | 33.5 33.6 | 33.6 | 97.2 96.5 | 96.9 | 6.4 6.4 | 6.4 | 6.2 | 3.1 3.1 | 3.1 | 6.3 | 4.2 4.8 | 4.5 | 6.1 | |
| | | | | Middle | 4.5 | 26.6 26.6 | 26.6 | 8.4 8.4 | 8.4 | 33.6 33.7 | 33.7 | 88.2 90.1 | 89.2 | 5.9 6.0 | 6.0 | | 6.0 | 8.1 8.1 | | 8.1 | 8.6 8.6 | | 8.6 |
| | | | | Bottom | 8 | 26.6 26.6 | 26.6 | 8.4 8.4 | 8.4 | 33.7 33.7 | 33.7 | 89.3 89.2 | 89.3 | 5.9 5.9 | 5.9 | | 5.9 | 7.7 7.8 | | 7.8 | 5.2 5.1 | | 5.2 |
| M1 | Sunny | Moderate | 14:48 | Surface | 1 | 26.9 26.8 | 26.9 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 94.8 93.9 | 94.4 | 6.3 6.2 | 6.3 | 6.3 | 3.2 3.3 | 3.3 | 3.7 | 4.0 4.0 | 4.0 | 4.2 | |
| | | | | Middle | 3 | 26.8 26.7 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 93.1 92.2 | 92.7 | 6.2 6.1 | 6.2 | | 6.2 | 3.2 3.5 | | 3.4 | 4.1 4.2 | | 4.2 |
| | | | | Bottom | 5 | 26.6 26.6 | 26.6 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 89.7 89.5 | 89.6 | 6.0 6.0 | 6.0 | | 6.0 | 4.4 4.5 | | 4.5 | 4.1 4.4 | | 4.3 |
| M2 | Sunny | Moderate | 14:32 | Surface | 1 | 26.9 26.9 | 26.9 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 94.2 94.0 | 94.1 | 6.2 6.2 | 6.2 | 6.1 | 4.7 4.5 | 4.6 | 4.0 | 3.2 3.4 | 3.3 | 4.8 | |
| | | | | Middle | 6 | 26.6 26.6 | 26.6 | 8.5 8.4 | 8.5 | 33.6 33.6 | 33.6 | 90.7 90.8 | 90.8 | 6.0 6.0 | 6.0 | | 6.0 | 3.6 3.7 | | 3.7 | 6.1 6.1 | | 6.1 |
| | | | | Bottom | 11 | 26.6 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.3 91.4 | 91.4 | 6.1 6.1 | 6.1 | | 6.1 | 4.0 3.6 | | 3.8 | 4.9 4.8 | | 4.9 |
| M3 | Sunny | Moderate | 15:05 | Surface | 1 | 26.8 26.9 | 26.9 | 8.5 8.5 | 8.5 | 33.4 33.4 | 33.4 | 93.8 94.0 | 93.9 | 6.2 6.2 | 6.2 | 6.2 | 3.2 3.0 | 3.1 | 3.4 | 5.0 4.8 | 4.9 | 4.9 | |
| | | | | Middle | 4 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.5 33.6 | 33.6 | 91.9 91.7 | 91.8 | 6.1 6.1 | 6.1 | | 6.1 | 3.6 3.5 | | 3.6 | 5.1 5.0 | | 5.1 |
| | | | | Bottom | 7 | 26.6 26.6 | 26.6 | 8.5 8.4 | 8.5 | 33.6 33.6 | 33.6 | 91.0 88.1 | 89.6 | 6.1 5.9 | 6.0 | | 6.0 | 3.4 3.5 | | 3.5 | 4.8 4.7 | | 4.8 |
| M4 | Sunny | Moderate | 14:24 | Surface | 1 | 26.8 26.8 | 26.8 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 91.9 91.4 | 91.7 | 6.1 6.1 | 6.1 | 6.1 | 4.2 4.3 | 4.3 | 4.2 | 4.5 4.5 | 4.5 | 4.3 | |
| | | | | Middle | 5 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.8 92.1 | 92.0 | 6.1 6.1 | 6.1 | | 6.1 | 4.0 3.8 | | 3.9 | 5.2 5.3 | | 5.3 |
| | | | | Bottom | 9 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.7 91.7 | 91.7 | 6.1 6.1 | 6.1 | | 6.1 | 4.4 4.5 | | 4.5 | 3.0 3.1 | | 3.1 |
| M5 | Sunny | Moderate | 15:26 | Surface | 1 | 27.0 26.5 | 26.8 | 8.4 8.5 | 8.5 | 33.6 33.6 | 33.6 | 94.1 88.7 | 91.4 | 6.2 5.9 | 6.1 | 6.0 | 4.6 4.6 | 4.6 | 6.4 | 4.6 13.3 | 4.6 | 7.7 | |
| | | | | Middle | 6 | 26.7 26.6 | 26.7 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 89.1 89.0 | 89.1 | 5.9 5.9 | 5.9 | | 5.9 | 6.9 6.9 | | 6.9 | 13.5 4.8 | | 13.5 |
| | | | | Bottom | 11 | 26.6 26.6 | 26.6 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 88.4 88.4 | 88.4 | 5.9 5.9 | 5.9 | | 5.9 | 7.7 7.8 | | 7.8 | 4.9 4.9 | | 4.9 |
| M6 | Sunny | Moderate | 15:23 | Surface | - | - | - | - | - | - | - | - | - | - | - | 6.1 | - | - | 5.0 | - | - | 4.9 | |
| | | | | Middle | 2 | 26.7 26.8 | 26.8 | 8.4 8.4 | 8.4 | 33.6 33.6 | 33.6 | 92.0 90.7 | 91.4 | 6.1 6.0 | 6.1 | | 6.1 | 5.0 5.0 | | 5.0 | 4.8 5.0 | | 4.9 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 23 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 8.4 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 9.1 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.8 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.2 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.8 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.2 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 23 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|------------|-------------------------|------------|------------|------------|--------------|------|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | | | |
| C1 | Sunny | Moderate | 10:02 | Surface | 1 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 92.3 92.0 | 92.2 | 6.1 6.1 | 6.1 | 6.1 | 6.1 | 3.7 3.6 | 3.7 | 4.9 | 4.4 4.5 | 4.5 | 5.7 | |
| | | | | Middle | 9.5 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 92.4 92.5 | 92.5 | 6.1 6.1 | 6.1 | 6.1 | | 6.1 | 4.1 4.1 | | 4.1 | 6.0 6.3 | | 6.2 |
| | | | | Bottom | 18 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.8 33.8 | 33.8 | 91.7 91.6 | 91.7 | 6.1 6.1 | 6.1 | 6.1 | | 6.1 | 6.8 6.8 | | 6.8 | 6.4 6.3 | | 6.4 |
| C2 | Sunny | Moderate | 08:45 | Surface | 1 | 26.8 26.7 | 26.8 | 8.4 8.4 | 8.4 | 33.6 33.7 | 33.7 | 92.1 92.2 | 92.2 | 6.1 6.1 | 6.1 | 6.1 | 3.3 3.3 | 3.3 | 4.4 | 4.8 4.8 | 4.8 | 4.8 | | |
| | | | | Middle | 17 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 92.1 92.1 | 92.1 | 6.1 6.1 | 6.1 | | 6.1 | 6.1 | | 3.7 3.6 | 3.7 | | 4.5 4.6 | 4.6 |
| | | | | Bottom | 33 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.9 92.0 | 92.0 | 6.1 6.1 | 6.1 | | 6.1 | 6.1 | | 6.8 5.5 | 6.2 | | 5.0 5.0 | 5.0 |
| G1 | Sunny | Moderate | 09:21 | Surface | 1 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.5 33.5 | 33.5 | 92.4 92.2 | 92.3 | 6.1 6.1 | 6.1 | 6.1 | 3.4 3.4 | 3.4 | 3.9 | 3.6 3.6 | 3.6 | 5.6 | | |
| | | | | Middle | 4 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 91.6 91.7 | 91.7 | 6.1 6.1 | 6.1 | | 6.1 | 6.1 | | 4.0 4.1 | 4.1 | | 8.5 8.4 | 8.5 |
| | | | | Bottom | 7 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 90.3 89.7 | 90.0 | 6.0 6.0 | 6.0 | | 6.0 | 6.0 | | 4.0 4.4 | 4.2 | | 4.6 4.5 | 4.6 |
| G2 | Sunny | Moderate | 09:11 | Surface | 1 | 26.8 26.7 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 92.1 91.6 | 91.9 | 6.1 6.1 | 6.1 | 6.1 | 3.8 4.0 | 3.9 | 4.3 | 4.6 4.5 | 4.6 | 5.4 | | |
| | | | | Middle | 5 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 90.3 90.2 | 90.3 | 6.0 6.0 | 6.0 | | 6.0 | 6.0 | | 4.2 4.5 | 4.4 | | 5.1 5.0 | 5.1 |
| | | | | Bottom | 9 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 89.5 89.4 | 89.5 | 6.0 5.9 | 6.0 | | 6.0 | 6.0 | | 4.6 4.5 | 4.6 | | 6.6 6.6 | 6.6 |
| G3 | Sunny | Moderate | 09:29 | Surface | 1 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.2 33.3 | 33.3 | 91.2 91.0 | 91.1 | 6.1 6.1 | 6.1 | 6.1 | 3.5 3.5 | 3.5 | 3.6 | 3.5 3.5 | 3.5 | 5.3 | | |
| | | | | Middle | 4 | 26.4 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 88.7 90.2 | 89.5 | 5.9 6.0 | 6.0 | | 6.0 | 6.0 | | 3.4 3.3 | 3.4 | | 6.6 6.4 | 6.5 |
| | | | | Bottom | 7 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 89.4 89.4 | 89.4 | 6.0 5.9 | 6.0 | | 6.0 | 6.0 | | 3.7 3.9 | 3.8 | | 5.7 5.8 | 5.8 |
| G4 | Sunny | Moderate | 09:41 | Surface | 1 | 26.8 26.7 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 92.0 91.9 | 92.0 | 6.1 6.1 | 6.1 | 6.1 | 3.2 3.1 | 3.2 | 3.3 | 4.2 4.1 | 4.2 | 5.2 | | |
| | | | | Middle | 4.5 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.5 91.5 | 91.5 | 6.1 6.1 | 6.1 | | 6.1 | 6.1 | | 3.3 3.3 | 3.3 | | 6.6 6.5 | 6.6 |
| | | | | Bottom | 8 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 89.4 89.0 | 89.2 | 6.0 5.9 | 6.0 | | 6.0 | 6.0 | | 3.4 3.5 | 3.5 | | 4.8 4.9 | 4.9 |
| M1 | Sunny | Moderate | 09:17 | Surface | 1 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 91.9 91.9 | 91.9 | 6.1 6.1 | 6.1 | 6.1 | 3.7 3.7 | 3.7 | 3.8 | 3.6 3.6 | 3.6 | 5.0 | | |
| | | | | Middle | 3 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 90.3 90.4 | 90.4 | 6.0 6.0 | 6.0 | | 6.0 | 6.0 | | 3.9 3.9 | 3.9 | | 6.3 6.4 | 6.4 |
| | | | | Bottom | 5 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 90.2 90.3 | 90.3 | 6.0 6.0 | 6.0 | | 6.0 | 6.0 | | 3.9 3.9 | 3.9 | | 5.1 5.1 | 5.1 |
| M2 | Sunny | Moderate | 09:03 | Surface | 1 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 92.6 92.4 | 92.5 | 6.1 6.1 | 6.1 | 6.1 | 4.0 3.9 | 4.0 | 4.6 | 3.1 3.1 | 3.1 | 4.2 | | |
| | | | | Middle | 6 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 90.2 90.3 | 90.3 | 6.0 6.0 | 6.0 | | 6.0 | 6.0 | | 5.1 5.0 | 5.1 | | 4.0 3.9 | 4.0 |
| | | | | Bottom | 11 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 89.3 89.1 | 89.2 | 5.9 5.9 | 5.9 | | 5.9 | 5.9 | | 4.4 4.8 | 4.6 | | 5.5 5.5 | 5.5 |
| M3 | Sunny | Moderate | 09:34 | Surface | 1 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.5 33.4 | 33.5 | 91.8 91.5 | 91.7 | 6.1 6.1 | 6.1 | 6.1 | 3.6 3.4 | 3.5 | 3.9 | 4.6 4.4 | 4.5 | 6.1 | | |
| | | | | Middle | 4 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 90.4 90.6 | 90.5 | 6.0 6.0 | 6.0 | | 6.0 | 6.0 | | 3.8 4.0 | 3.9 | | 7.1 7.1 | 7.1 |
| | | | | Bottom | 7 | 26.4 26.4 | 26.4 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 88.7 88.8 | 88.8 | 5.9 5.9 | 5.9 | | 5.9 | 5.9 | | 4.5 4.2 | 4.4 | | 6.8 6.8 | 6.8 |
| M4 | Sunny | Moderate | 08:56 | Surface | 1 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 91.1 90.8 | 91.0 | 6.1 6.0 | 6.1 | 6.0 | 4.9 4.6 | 4.8 | 5.4 | 4.4 4.4 | 4.4 | 5.4 | | |
| | | | | Middle | 5 | 26.7 26.6 | 26.7 | 8.4 8.5 | 8.5 | 33.6 33.6 | 33.6 | 88.0 90.3 | 89.2 | 5.8 6.0 | 5.9 | | 5.9 | 5.9 | | 4.9 5.7 | 5.3 | | 7.2 7.3 | 7.3 |
| | | | | Bottom | 9 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 90.6 90.5 | 90.6 | 6.0 6.0 | 6.0 | | 6.0 | 6.0 | | 5.8 6.1 | 6.0 | | 4.5 4.7 | 4.6 |
| M5 | Sunny | Moderate | 09:54 | Surface | 1 | 26.9 26.9 | 26.9 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 91.4 91.0 | 91.2 | 6.1 6.0 | 6.1 | 6.1 | 3.2 3.2 | 3.2 | 4.9 | 4.3 4.7 | 4.5 | 6.2 | | |
| | | | | Middle | 6 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 90.3 90.4 | 90.4 | 6.0 6.0 | 6.0 | | 6.0 | 6.0 | | 3.9 3.9 | 3.8 | | 10.0 10.3 | 10.2 |
| | | | | Bottom | 11 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 90.3 90.2 | 90.3 | 6.0 6.0 | 6.0 | | 6.0 | 6.0 | | 7.8 7.7 | 7.8 | | 3.7 3.9 | 3.8 |
| M6 | Sunny | Moderate | 09:48 | Surface | - | - | - | - | - | - | - | - | - | - | - | 6.1 | - | - | 3.5 | - | - | 5.0 | | |
| | | | | Middle | 2 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 92.6 92.5 | 92.6 | 6.1 6.1 | 6.1 | | 6.1 | 6.1 | | 3.4 3.6 | 3.5 | | 4.9 5.0 | 5.0 |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | | - | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 23 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|--|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 8.2 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 8.8 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.4 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.4 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.7 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 8.3 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 25 October 2017**

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|------------|------------|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 16:24 | Surface | 1 | 26.5 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.6 33.7 | 33.7 | 96.6 95.2 | 95.9 | 6.4 6.3 | 6.4 | 6.4 | 3.2 3.2 | 3.2 | 3.8 | 3.8 3.9 | 3.9 | 5.1 |
| | | | | Middle | 9.5 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 94.9 95.0 | 95.0 | 6.3 6.3 | 6.3 | | 3.1 3.1 | 3.1 | | 3.1 7.8 | 7.9 | |
| | | | | Bottom | 18 | 26.4 26.4 | 26.4 | 8.5 8.5 | 8.5 | 33.8 33.8 | 33.8 | 92.7 92.8 | 92.8 | 6.2 6.2 | 6.2 | | 5.0 5.1 | 5.1 | | 5.1 | 3.6 3.5 | |
| C2 | Sunny | Moderate | 15:18 | Surface | 1 | 26.6 26.7 | 26.7 | 8.6 8.6 | 8.6 | 33.7 33.7 | 33.7 | 95.3 95.5 | 95.4 | 6.3 6.3 | 6.3 | 6.3 | 2.7 2.8 | 2.8 | 3.8 | 4.0 3.9 | 4.0 | 4.2 |
| | | | | Middle | 17 | 26.5 26.5 | 26.5 | 8.6 8.6 | 8.6 | 33.7 33.7 | 33.7 | 93.2 93.3 | 93.3 | 6.2 6.2 | 6.2 | | 3.4 3.4 | 3.4 | | 3.1 3.1 | 3.1 | |
| | | | | Bottom | 33 | 26.4 26.4 | 26.4 | 8.6 8.6 | 8.6 | 33.8 33.8 | 33.8 | 92.2 92.1 | 92.2 | 6.1 6.1 | 6.1 | | 5.1 5.5 | 5.3 | | 5.3 5.6 | 5.5 | |
| G1 | Sunny | Moderate | 15:50 | Surface | 1 | 26.9 26.9 | 26.9 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 96.7 96.9 | 96.8 | 6.4 6.4 | 6.4 | 6.3 | 2.9 2.9 | 2.9 | 4.2 | 3.9 4.0 | 4.0 | 5.5 |
| | | | | Middle | 4 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.4 91.5 | 91.5 | 6.1 6.1 | 6.1 | | 4.0 4.1 | 4.1 | | 6.3 6.2 | 6.3 | |
| | | | | Bottom | 7 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 90.2 90.5 | 90.4 | 6.0 6.0 | 6.0 | | 5.8 5.3 | 5.6 | | 6.2 6.2 | 6.2 | |
| G2 | Sunny | Moderate | 15:39 | Surface | 1 | 26.8 26.9 | 26.9 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 98.0 98.0 | 98.0 | 6.5 6.5 | 6.5 | 6.4 | 2.8 2.8 | 2.8 | 3.1 | 4.3 4.2 | 4.3 | 5.3 |
| | | | | Middle | 5 | 26.7 26.6 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 95.5 95.0 | 95.3 | 6.3 6.3 | 6.3 | | 2.6 2.6 | 2.6 | | 7.1 6.9 | 7.0 | |
| | | | | Bottom | 9 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.5 91.4 | 91.5 | 6.1 6.1 | 6.1 | | 4.0 4.0 | 4.0 | | 4.6 4.6 | 4.6 | |
| G3 | Sunny | Moderate | 15:57 | Surface | 1 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.1 33.0 | 33.1 | 93.0 93.0 | 93.0 | 6.2 6.2 | 6.2 | 6.2 | 3.6 3.6 | 3.6 | 4.2 | 4.1 4.2 | 4.2 | 4.9 |
| | | | | Middle | 4 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.5 33.5 | 33.5 | 92.8 93.3 | 93.1 | 6.2 6.2 | 6.2 | | 3.6 3.5 | 3.6 | | 5.8 5.6 | 5.7 | |
| | | | | Bottom | 7 | 26.6 26.8 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.1 | 33.4 | 88.3 93.3 | 90.8 | 5.9 6.2 | 6.1 | | 5.3 5.6 | 5.5 | | 4.8 4.8 | 4.8 | |
| G4 | Sunny | Moderate | 16:09 | Surface | 1 | 26.9 26.9 | 26.9 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 97.1 97.4 | 97.3 | 6.4 6.5 | 6.5 | 6.4 | 2.9 2.8 | 2.9 | 3.9 | 2.9 2.9 | 2.9 | 3.9 |
| | | | | Middle | 4.5 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 95.3 94.9 | 95.1 | 6.3 6.3 | 6.3 | | 3.0 3.1 | 3.1 | | 3.6 3.5 | 3.6 | |
| | | | | Bottom | 8 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 86.1 87.1 | 86.6 | 5.7 5.8 | 5.8 | | 5.8 5.8 | 5.8 | | 5.3 5.3 | 5.3 | |
| M1 | Sunny | Moderate | 15:45 | Surface | 1 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 97.2 96.3 | 96.8 | 6.4 6.4 | 6.4 | 6.3 | 3.2 3.6 | 3.4 | 4.1 | 4.1 4.1 | 4.1 | 4.4 |
| | | | | Middle | 3 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 93.1 93.0 | 93.1 | 6.2 6.2 | 6.2 | | 3.9 3.9 | 3.9 | | 4.9 4.9 | 4.9 | |
| | | | | Bottom | 5 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 91.6 91.6 | 91.6 | 6.1 6.1 | 6.1 | | 5.0 5.2 | 5.1 | | 4.2 4.2 | 4.2 | |
| M2 | Sunny | Moderate | 15:32 | Surface | 1 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 98.3 98.1 | 98.2 | 6.5 6.5 | 6.5 | 6.4 | 2.7 2.6 | 2.7 | 3.2 | 3.2 3.3 | 3.3 | 3.5 |
| | | | | Middle | 6 | 26.6 26.5 | 26.6 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 93.8 93.8 | 93.8 | 6.2 6.2 | 6.2 | | 2.7 2.5 | 2.6 | | 3.9 4.0 | 4.0 | |
| | | | | Bottom | 11 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.4 91.3 | 91.4 | 6.1 6.1 | 6.1 | | 4.3 4.4 | 4.4 | | 3.1 3.2 | 3.2 | |
| M3 | Sunny | Moderate | 16:02 | Surface | 1 | 26.9 26.9 | 26.9 | 8.5 8.5 | 8.5 | 33.4 33.4 | 33.4 | 94.3 93.0 | 93.7 | 6.2 6.2 | 6.2 | 6.2 | 3.4 3.5 | 3.5 | 3.8 | 2.6 2.6 | 2.6 | 2.7 |
| | | | | Middle | 4 | 26.9 26.9 | 26.9 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 94.2 94.4 | 94.3 | 6.2 6.2 | 6.2 | | 3.1 3.2 | 3.2 | | 2.9 2.9 | 2.9 | |
| | | | | Bottom | 7 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 82.9 83.2 | 83.1 | 5.5 5.5 | 5.5 | | 4.9 4.2 | 4.6 | | 2.6 2.7 | 2.7 | |
| M4 | Sunny | Moderate | 15:26 | Surface | 1 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 96.0 95.8 | 95.9 | 6.4 6.4 | 6.4 | 6.4 | 2.8 2.9 | 2.9 | 2.9 | 4.1 4.1 | 4.1 | 4.0 |
| | | | | Middle | 5 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 94.7 95.1 | 94.9 | 6.3 6.3 | 6.3 | | 2.8 2.7 | 2.8 | | 3.5 3.5 | 3.5 | |
| | | | | Bottom | 9 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 93.7 93.4 | 93.6 | 6.2 6.2 | 6.2 | | 2.9 3.0 | 3.0 | | 4.4 4.4 | 4.4 | |
| M5 | Sunny | Moderate | 16:19 | Surface | 1 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.6 33.7 | 33.7 | 93.8 93.3 | 93.6 | 6.3 6.2 | 6.3 | 6.2 | 4.6 4.6 | 4.6 | 5.7 | 4.4 4.6 | 4.5 | 5.9 |
| | | | | Middle | 6 | 26.4 26.4 | 26.4 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.1 91.0 | 91.1 | 6.1 6.1 | 6.1 | | 6.5 6.4 | 6.5 | | 8.4 8.7 | 8.6 | |
| | | | | Bottom | 11 | 26.4 26.4 | 26.4 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.2 91.0 | 91.1 | 6.1 6.1 | 6.1 | | 6.1 6.1 | 6.1 | | 4.6 4.5 | 4.6 | |
| M6 | Sunny | Moderate | 16:15 | Surface | - | - | - | - | - | - | - | - | - | - | - | 6.3 | - | - | 2.5 | - | - | 3.9 |
| | | | | Middle | 2.4 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 96.9 94.4 | 95.7 | 6.4 6.2 | 6.3 | | 2.6 2.4 | 2.5 | | 3.8 3.9 | 3.9 | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 25 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 6.4 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 6.9 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 4.8 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 5.2 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 4.8 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 5.2 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 25 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | | | | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|--------------|-------------------------|------------|-----|----------------|-------------------|-----|-------------------------|-------------------|-----|-----|-----|-----|--------------|------------|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | | | | | | |
| C1 | Sunny | Moderate | 11:39 | Surface | 1 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 94.0 93.2 | 93.6 | 6.2 6.2 | 6.2 | 6.3 | 3.8 3.0 3.1 | 3.8 | 4.3 | 4.7 2.9 2.9 | 4.7 | 4.7 | | | | | |
| | | | | Middle | 9.5 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 94.5 94.4 | 94.5 | 6.3 6.3 | 6.3 | | | | | | | | 6.2 | 6.2 | 6.0 | 5.8 5.8 | 5.9 |
| | | | | Bottom | 18 | 26.4 26.4 | 26.4 | 8.5 8.5 | 8.5 | 33.8 33.8 | 33.8 | 92.9 92.9 | 92.9 | 6.2 6.2 | 6.2 | | | | | | | | | | | | |
| C2 | Sunny | Moderate | 10:34 | Surface | 1 | 26.6 26.6 | 26.6 | 8.6 8.6 | 8.6 | 33.6 33.6 | 33.6 | 92.6 92.6 | 92.6 | 6.2 6.2 | 6.2 | 6.2 | 3.1 3.1 | 3.1 | 5.5 | 4.1 4.1 | 4.1 | | | | | | |
| | | | | Middle | 17.5 | 26.5 26.5 | 26.5 | 8.6 8.6 | 8.6 | 33.8 33.8 | 33.8 | 91.6 91.7 | 91.7 | 6.1 6.1 | 6.1 | | | | | | | 6.1 | 7.1 | 7.1 | 5.4 5.3 | 5.4 | |
| | | | | Bottom | 34 | 26.5 26.4 | 26.5 | 8.6 8.6 | 8.6 | 33.8 33.8 | 33.8 | 91.2 91.4 | 91.3 | 6.1 6.1 | 6.1 | | | | | | | | | | | | 6.1 |
| G1 | Sunny | Moderate | 11:07 | Surface | 1 | 26.7 26.7 | 26.7 | 8.6 8.6 | 8.6 | 33.5 33.6 | 33.6 | 93.1 93.0 | 93.1 | 6.2 6.2 | 6.2 | 6.2 | 3.1 3.2 | 3.2 | 3.1 | 5.1 5.0 | 5.1 | | | | | | |
| | | | | Middle | 4 | 26.7 26.7 | 26.7 | 8.6 8.6 | 8.6 | 33.6 33.6 | 33.6 | 93.1 93.2 | 93.2 | 6.2 6.2 | 6.2 | | | | | | | 6.1 | 3.0 | 3.0 | 4.4 4.4 | 4.4 | |
| | | | | Bottom | 7 | 26.6 26.6 | 26.6 | 8.6 8.6 | 8.6 | 33.6 33.6 | 33.6 | 91.2 91.3 | 91.3 | 6.1 6.1 | 6.1 | | | | | | | | | | | | 6.1 |
| G2 | Sunny | Moderate | 10:56 | Surface | 1 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.5 33.5 | 33.5 | 93.6 93.5 | 93.6 | 6.2 6.2 | 6.2 | 6.2 | 2.8 2.7 | 2.8 | 3.1 | 5.5 5.4 | 5.5 | | | | | | |
| | | | | Middle | 5 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 92.2 92.2 | 92.2 | 6.1 6.1 | 6.1 | | | | | | | 6.1 | 3.1 | 3.1 | 3.2 3.1 | 3.2 | |
| | | | | Bottom | 9 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.1 91.3 | 91.2 | 6.1 6.1 | 6.1 | | | | | | | | | | | | 6.1 |
| G3 | Sunny | Moderate | 11:13 | Surface | 1 | 26.6 26.6 | 26.6 | 8.6 8.6 | 8.6 | 33.4 33.1 | 33.3 | 90.2 90.3 | 90.3 | 6.0 6.0 | 6.0 | 6.0 | 6.1 6.0 | 6.1 | 8.1 | 5.0 4.8 | 4.9 | | | | | | |
| | | | | Middle | 4 | 26.5 26.5 | 26.5 | 8.6 8.6 | 8.6 | 33.7 33.7 | 33.7 | 88.4 88.4 | 88.4 | 5.9 5.9 | 5.9 | | | | | | | 5.8 | 7.2 | 7.2 | 14.9 14.7 | 14.8 | |
| | | | | Bottom | 7 | 26.5 26.5 | 26.5 | 8.6 8.6 | 8.6 | 33.7 33.7 | 33.7 | 87.7 87.6 | 87.7 | 5.8 5.8 | 5.8 | | | | | | | | | | | | 5.8 |
| G4 | Sunny | Moderate | 11:24 | Surface | 1 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 91.0 90.6 | 90.8 | 6.0 6.0 | 6.0 | 6.0 | 3.0 2.9 | 3.0 | 4.0 | 4.1 4.2 | 4.2 | | | | | | |
| | | | | Middle | 4.5 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 90.0 90.0 | 90.0 | 6.0 6.0 | 6.0 | | | | | | | 5.9 | 5.8 | 5.9 | 6.2 6.1 | 6.2 | |
| | | | | Bottom | 8 | 26.5 26.5 | 26.5 | 8.6 8.6 | 8.6 | 33.7 33.7 | 33.7 | 88.7 88.5 | 88.6 | 5.9 5.9 | 5.9 | | | | | | | | | | | | 5.9 |
| M1 | Sunny | Moderate | 11:03 | Surface | 1 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 92.9 92.7 | 92.8 | 6.2 6.2 | 6.2 | 6.2 | 3.4 3.5 | 3.5 | 3.3 | 3.9 3.8 | 3.9 | | | | | | |
| | | | | Middle | 3 | 26.6 26.6 | 26.6 | 8.6 8.5 | 8.6 | 33.6 33.6 | 33.6 | 92.4 92.5 | 92.5 | 6.1 6.2 | 6.2 | | | | | | | 6.1 | 3.2 | 3.2 | 4.5 4.6 | 4.6 | |
| | | | | Bottom | 5 | 26.5 26.5 | 26.5 | 8.6 8.6 | 8.6 | 33.7 33.7 | 33.7 | 91.2 91.3 | 91.3 | 6.1 6.1 | 6.1 | | | | | | | | | | | | 6.1 |
| M2 | Sunny | Moderate | 10:49 | Surface | 1 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.7 33.6 | 33.7 | 93.8 93.8 | 93.8 | 6.2 6.2 | 6.2 | 6.2 | 3.1 3.1 | 3.1 | 3.7 | 3.7 3.8 | 3.8 | | | | | | |
| | | | | Middle | 6 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 91.9 92.0 | 92.0 | 6.1 6.1 | 6.1 | | | | | | | 6.0 | 4.9 | 4.9 | 2.6 2.6 | 2.6 | |
| | | | | Bottom | 11 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 89.7 89.3 | 89.5 | 6.0 5.9 | 6.0 | | | | | | | | | | | | 6.0 |
| M3 | Sunny | Moderate | 11:17 | Surface | 1 | 26.7 26.6 | 26.7 | 8.6 8.6 | 8.6 | 33.3 33.6 | 33.5 | 90.6 90.4 | 90.5 | 6.0 6.0 | 6.0 | 6.0 | 5.0 5.2 | 5.1 | 5.4 | 3.1 3.2 | 3.2 | | | | | | |
| | | | | Middle | 4 | 26.6 26.6 | 26.6 | 8.6 8.6 | 8.6 | 33.6 33.6 | 33.6 | 90.4 90.5 | 90.5 | 6.0 6.0 | 6.0 | | | | | | | 5.8 | 4.8 | 4.9 | 6.5 6.7 | 6.6 | |
| | | | | Bottom | 7 | 26.5 26.5 | 26.5 | 8.6 8.6 | 8.6 | 33.7 33.7 | 33.7 | 87.0 86.7 | 86.9 | 5.8 5.8 | 5.8 | | | | | | | | | | | | 5.8 |
| M4 | Sunny | Moderate | 10:42 | Surface | 1 | 26.6 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 93.1 93.0 | 93.1 | 6.2 6.2 | 6.2 | 6.2 | 3.6 3.5 | 3.6 | 3.8 | 3.6 3.8 | 3.7 | | | | | | |
| | | | | Middle | 5 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.4 91.4 | 91.4 | 6.1 6.1 | 6.1 | | | | | | | 6.1 | 4.2 | 4.2 | 4.9 5.0 | 5.0 | |
| | | | | Bottom | 9 | 26.5 26.5 | 26.5 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.3 91.4 | 91.4 | 6.1 6.1 | 6.1 | | | | | | | | | | | | 6.1 |
| M5 | Sunny | Moderate | 11:34 | Surface | 1 | 26.7 26.7 | 26.7 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 93.8 93.3 | 93.6 | 6.2 6.2 | 6.2 | 6.2 | 2.9 2.9 | 2.9 | 4.9 | 4.4 4.4 | 4.4 | | | | | | |
| | | | | Middle | 6 | 26.5 26.6 | 26.6 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 91.0 91.3 | 91.2 | 6.1 6.1 | 6.1 | | | | | | | 6.2 | 5.4 | 5.4 | 8.2 8.0 | 8.1 | |
| | | | | Bottom | 11 | 26.4 26.3 | 26.4 | 8.5 8.5 | 8.5 | 33.7 33.7 | 33.7 | 91.7 92.4 | 92.1 | 6.1 6.2 | 6.2 | | | | | | | | | | | | 6.2 |
| M6 | Sunny | Moderate | 11:29 | Surface | - | - | - | - | - | - | - | - | - | - | 6.2 | - | - | 3.2 | - | - | | | | | | | |
| | | | | Middle | 2.1 | 26.8 26.8 | 26.8 | 8.5 8.5 | 8.5 | 33.6 33.6 | 33.6 | 93.7 93.4 | 93.6 | 6.2 6.2 | | | | | | | 6.2 | 3.2 | 3.2 | 3.8 | 3.8 | | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | | | | | | | - | | | | | - | - |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 25 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 7.2 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 7.8 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.6 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.1 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.6 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.1 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.1 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.7 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 27 October 2017

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | | |
|----------|-------------------|-----------------|---------------|-----------|------------------|--------------|-------|------------|--------------|--------------|-------------------|----------------|-------------------------|------------|-----|----------------|------------|-----|-------------------------|------------|-----|-----|
| | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* | |
| C1 | Sunny | Moderate | 16:54 | Surface | 1 | 29.3 29.3 | 29.3 | 8.6 8.6 | 8.6 | 29.6 29.6 | 29.6 | 102.3 101.4 | 101.9 | 6.7 6.6 | 6.7 | 6.0 | 2.3 2.3 | 2.3 | 5.0 | 5.3 5.3 | 5.3 | 5.3 |
| | | | | Middle | 9.5 | 28.1 28.1 | 28.1 | 8.4 8.4 | 8.4 | 30.4 30.4 | 30.4 | 79.7 79.4 | 79.6 | 5.3 5.2 | 5.3 | | 3.0 2.9 | 3.0 | | 5.0 5.6 | 5.5 | |
| | | | | Bottom | 18 | 24.7 24.9 | 24.8 | 8.1 8.2 | 8.2 | 34.9 34.6 | 34.8 | 63.2 64.4 | 63.8 | 4.3 4.4 | 4.4 | | 9.8 9.7 | 9.8 | | 5.0 5.2 | 5.1 | |
| C2 | Sunny | Moderate | 15:37 | Surface | 1 | 28.6 28.6 | 28.6 | 8.5 8.5 | 8.5 | 30.0 30.0 | 30.0 | 92.8 93.1 | 93.0 | 6.1 6.1 | 6.1 | 5.4 | 2.3 2.5 | 2.4 | 5.1 | 5.7 5.6 | 5.7 | 4.7 |
| | | | | Middle | 17 | 27.6 27.4 | 27.5 | 8.4 8.3 | 8.4 | 30.8 31.1 | 31.0 | 71.0 68.0 | 69.5 | 4.7 4.5 | 4.6 | | 5.0 4.7 | 4.9 | | 2.9 2.9 | 2.9 | |
| | | | | Bottom | 33 | 26.9 26.9 | 26.9 | 8.3 8.3 | 8.3 | 31.8 31.7 | 31.8 | 65.7 66.4 | 66.1 | 4.4 4.4 | 4.4 | | 7.8 8.4 | 8.1 | | 5.5 5.3 | 5.4 | |
| G1 | Sunny | Moderate | 16:16 | Surface | 1 | 28.4 28.4 | 28.4 | 8.4 8.4 | 8.4 | 30.1 30.1 | 30.1 | 87.8 87.4 | 87.6 | 5.8 5.8 | 5.8 | 5.7 | 3.0 3.1 | 3.1 | 3.0 | 3.9 4.0 | 4.0 | 5.5 |
| | | | | Middle | 4 | 28.2 28.2 | 28.2 | 8.4 8.4 | 8.4 | 30.2 30.2 | 30.2 | 84.1 84.5 | 84.3 | 5.6 5.6 | 5.6 | | 2.6 2.8 | 2.7 | | 7.0 7.2 | 7.1 | |
| | | | | Bottom | 7 | 28.0 27.9 | 28.0 | 8.4 8.4 | 8.4 | 30.3 30.5 | 30.4 | 79.7 76.3 | 78.0 | 5.3 5.1 | 5.2 | | 3.1 3.1 | 3.1 | | 5.4 5.4 | 5.4 | |
| G2 | Sunny | Moderate | 16:06 | Surface | 1 | 28.8 28.8 | 28.8 | 8.5 8.5 | 8.5 | 29.8 29.8 | 29.8 | 98.2 97.1 | 97.7 | 6.4 6.4 | 6.4 | 6.0 | 2.4 2.5 | 2.5 | 2.7 | 5.5 5.5 | 5.5 | 5.1 |
| | | | | Middle | 4.5 | 28.3 28.3 | 28.3 | 8.4 8.4 | 8.4 | 30.2 30.2 | 30.2 | 84.7 85.4 | 85.1 | 5.6 5.6 | 5.6 | | 2.9 2.9 | 2.9 | | 4.9 4.6 | 4.8 | |
| | | | | Bottom | 8 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 30.5 30.5 | 30.5 | 77.5 77.2 | 77.4 | 5.1 5.1 | 5.1 | | 2.8 2.6 | 2.7 | | 5.0 4.9 | 5.0 | |
| G3 | Sunny | Moderate | 16:23 | Surface | 1 | 28.5 28.6 | 28.6 | 8.5 8.5 | 8.5 | 29.7 29.7 | 29.7 | 95.3 93.6 | 94.5 | 6.3 6.2 | 6.3 | 5.7 | 2.6 2.5 | 2.6 | 4.9 | 4.5 4.6 | 4.6 | 4.5 |
| | | | | Middle | 4 | 28.1 28.1 | 28.1 | 8.4 8.4 | 8.4 | 30.3 30.2 | 30.3 | 76.1 76.3 | 76.2 | 5.0 5.0 | 5.0 | | 4.2 4.1 | 4.2 | | 4.5 4.6 | 4.6 | |
| | | | | Bottom | 7 | 27.7 27.7 | 27.7 | 8.3 8.4 | 8.4 | 30.6 30.6 | 30.6 | 66.5 65.6 | 66.1 | 4.4 4.4 | 4.4 | | 7.8 8.0 | 7.9 | | 4.3 4.5 | 4.4 | |
| G4 | Sunny | Moderate | 16:36 | Surface | 1 | 28.7 28.7 | 28.7 | 8.5 8.5 | 8.5 | 29.9 29.9 | 29.9 | 92.6 92.1 | 92.4 | 6.1 6.0 | 6.1 | 5.8 | 2.8 2.9 | 2.9 | 3.9 | 4.1 4.2 | 4.2 | 4.8 |
| | | | | Middle | 4.5 | 28.1 28.1 | 28.1 | 8.4 8.4 | 8.4 | 30.3 30.3 | 30.3 | 82.3 82.1 | 82.2 | 5.4 5.4 | 5.4 | | 2.8 2.8 | 2.8 | | 4.3 4.3 | 4.3 | |
| | | | | Bottom | 8 | 27.8 27.8 | 27.8 | 8.4 8.4 | 8.4 | 30.6 30.6 | 30.6 | 71.1 71.8 | 71.5 | 4.7 4.8 | 4.8 | | 6.1 5.8 | 6.0 | | 5.7 5.8 | 5.8 | |
| M1 | Sunny | Moderate | 16:12 | Surface | 1 | 28.6 28.6 | 28.6 | 8.5 8.5 | 8.5 | 29.8 29.8 | 29.8 | 92.8 91.6 | 92.2 | 6.1 6.0 | 6.1 | 5.9 | 2.8 2.8 | 2.8 | 3.2 | 4.5 4.8 | 4.7 | 4.6 |
| | | | | Middle | 3 | 28.3 28.2 | 28.3 | 8.4 8.4 | 8.4 | 30.1 30.2 | 30.2 | 84.7 82.9 | 83.8 | 5.6 5.5 | 5.6 | | 3.4 3.5 | 3.5 | | 5.1 5.1 | 5.1 | |
| | | | | Bottom | 5 | 28.1 28.1 | 28.1 | 8.4 8.4 | 8.4 | 30.4 30.3 | 30.4 | 79.5 79.9 | 79.7 | 5.3 5.3 | 5.3 | | 3.2 3.4 | 3.3 | | 4.0 4.2 | 4.1 | |
| M2 | Sunny | Moderate | 15:51 | Surface | 1 | 28.9 28.9 | 28.9 | 8.5 8.5 | 8.5 | 29.7 29.7 | 29.7 | 100.1 98.8 | 99.5 | 6.6 6.5 | 6.6 | 6.2 | 2.4 2.5 | 2.5 | 2.9 | 3.3 3.2 | 3.3 | 4.5 |
| | | | | Middle | 5.5 | 28.3 28.3 | 28.3 | 8.4 8.4 | 8.4 | 30.1 30.1 | 30.1 | 85.8 86.7 | 86.3 | 5.7 5.7 | 5.7 | | 2.6 2.6 | 2.6 | | 4.8 4.6 | 4.7 | |
| | | | | Bottom | 10 | 27.6 27.7 | 27.7 | 8.4 8.4 | 8.4 | 30.8 30.7 | 30.8 | 70.8 72.2 | 71.5 | 4.7 4.8 | 4.8 | | 3.3 4.1 | 3.7 | | 5.6 5.4 | 5.5 | |
| M3 | Sunny | Moderate | 16:27 | Surface | 1 | 28.6 28.7 | 28.7 | 8.5 8.5 | 8.5 | 29.6 29.4 | 29.5 | 94.8 94.7 | 94.8 | 6.2 6.2 | 6.2 | 5.7 | 2.6 2.5 | 2.6 | 3.3 | 5.2 5.4 | 5.3 | 6.3 |
| | | | | Middle | 4 | 28.1 28.1 | 28.1 | 8.4 8.4 | 8.4 | 30.2 30.2 | 30.2 | 78.4 78.7 | 78.6 | 5.2 5.2 | 5.2 | | 3.9 3.8 | 3.9 | | 8.5 8.4 | 8.5 | |
| | | | | Bottom | 7 | 27.7 27.9 | 27.8 | 8.3 8.4 | 8.4 | 30.6 30.6 | 30.6 | 66.5 74.3 | 70.4 | 4.4 4.9 | 4.7 | | 3.4 3.4 | 3.4 | | 5.2 5.2 | 5.2 | |
| M4 | Sunny | Moderate | 15:44 | Surface | 1 | 28.8 28.8 | 28.8 | 8.5 8.5 | 8.5 | 29.8 29.8 | 29.8 | 98.9 98.2 | 98.6 | 6.5 6.4 | 6.5 | 6.3 | 2.5 2.5 | 2.5 | 2.6 | 3.2 3.2 | 3.2 | 4.1 |
| | | | | Middle | 5 | 28.5 28.7 | 28.6 | 8.5 8.5 | 8.5 | 30.0 29.8 | 29.9 | 90.5 95.1 | 92.8 | 6.0 6.2 | 6.1 | | 2.6 2.5 | 2.6 | | 4.2 4.1 | 4.2 | |
| | | | | Bottom | 9 | 28.5 28.6 | 28.6 | 8.5 8.5 | 8.5 | 30.0 29.9 | 30.0 | 90.3 92.9 | 91.6 | 5.9 6.1 | 6.0 | | 2.6 2.5 | 2.6 | | 4.7 5.0 | 4.9 | |
| M5 | Sunny | Moderate | 16:47 | Surface | 1 | 28.6 28.6 | 28.6 | 8.4 8.4 | 8.4 | 30.0 30.0 | 30.0 | 86.0 86.9 | 86.5 | 5.6 5.7 | 5.7 | 5.7 | 2.8 2.6 | 2.7 | 3.8 | 5.2 5.1 | 5.2 | 6.4 |
| | | | | Middle | 6 | 28.4 28.3 | 28.4 | 8.4 8.4 | 8.4 | 30.1 30.2 | 30.2 | 86.2 85.2 | 85.7 | 5.7 5.6 | 5.7 | | 2.6 2.7 | 2.7 | | 9.0 8.7 | 8.9 | |
| | | | | Bottom | 11 | 27.9 27.9 | 27.9 | 8.4 8.4 | 8.4 | 30.5 30.6 | 30.6 | 74.8 73.3 | 74.1 | 5.0 4.9 | 5.0 | | 5.8 5.9 | 5.9 | | 5.2 5.0 | 5.1 | |
| M6 | Sunny | Moderate | 16:42 | Surface | - | - | - | - | - | - | - | - | - | - | - | 5.7 | - | - | 3.5 | - | - | 6.8 |
| | | | | Middle | 2.2 | 28.2 28.2 | 28.2 | 8.4 8.4 | 8.4 | 30.2 30.2 | 30.2 | 86.0 85.8 | 85.9 | 5.7 5.7 | 5.7 | | 3.5 3.5 | 3.5 | | 6.9 6.6 | 6.8 | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | | - | - | | - | - | |

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 27 October 2017 (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|--|--|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 11.8 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 12.7 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.9 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.9 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.1 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 30 October 2017**

(Mid-Ebb Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | |
|----------|-------------------|-----------------|---------------|-----------|-----|------------------|---------|------------|---------|--------------|---------|-------------------|---------|-------------------------|---------|-----|----------------|---------|-----|-------------------------|---------|-----|
| | | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* |
| C1 | Sunny | Moderate | 09:28 | Surface | 1 | 25.8 25.8 | 25.8 | 6.6 6.6 | 6.6 | 33.3 33.3 | 33.3 | 100.4 100.4 | 100.4 | 6.8 6.8 | 6.8 | 6.8 | 1.4 1.3 | 1.4 | 1.3 | 3.5 3.6 | 3.6 | 4.6 |
| | | | | Middle | 9.5 | 25.8 25.8 | 25.8 | 6.5 6.7 | 6.6 | 33.3 33.2 | 33.3 | 99.7 99.3 | 99.5 | 6.7 6.7 | 6.7 | 6.7 | 1.1 1.3 | 1.2 | | 4.9 4.8 | 4.9 | |
| | | | | Bottom | 18 | 25.8 25.8 | 25.8 | 6.6 6.7 | 6.7 | 33.3 33.3 | 33.3 | 99.0 99.0 | 99.0 | 6.7 6.7 | 6.7 | 6.7 | 1.3 1.2 | 1.3 | | 5.2 5.5 | 5.4 | |
| C2 | Sunny | Moderate | 08:14 | Surface | 1 | 25.8 25.7 | 25.8 | 5.3 6.1 | 5.7 | 32.9 32.2 | 32.9 | 92.4 92.4 | 92.4 | 6.3 6.3 | 6.3 | 6.3 | 1.1 1.1 | 1.1 | 2.6 | 6.0 6.0 | 6.0 | 5.9 |
| | | | | Middle | 17 | 26.0 26.0 | 26.0 | 5.4 6.2 | 5.8 | 33.2 33.2 | 33.2 | 93.4 93.3 | 93.4 | 6.3 6.3 | 6.3 | 6.3 | 2.0 1.9 | 2.0 | | 7.0 7.1 | 7.1 | |
| | | | | Bottom | 33 | 26.0 26.0 | 26.0 | 5.8 6.2 | 6.0 | 33.2 33.2 | 33.2 | 92.3 92.3 | 92.3 | 6.2 6.2 | 6.2 | 6.2 | 4.8 4.6 | 4.7 | | 4.8 4.6 | 4.7 | |
| G1 | Sunny | Moderate | 08:47 | Surface | 1 | 25.7 25.7 | 25.7 | 6.4 6.5 | 6.5 | 33.2 33.2 | 33.2 | 92.9 94.4 | 93.7 | 6.3 6.4 | 6.4 | 6.4 | 2.0 2.1 | 2.1 | 1.9 | 4.4 4.5 | 4.5 | 3.7 |
| | | | | Middle | 4 | 25.7 25.7 | 25.7 | 6.4 6.6 | 6.5 | 33.2 33.2 | 33.2 | 92.5 93.6 | 93.1 | 6.3 6.3 | 6.3 | 6.3 | 1.9 1.8 | 1.9 | | 3.9 3.8 | 3.9 | |
| | | | | Bottom | 7 | 25.7 25.7 | 25.7 | 6.5 6.6 | 6.6 | 33.2 33.2 | 33.2 | 92.2 93.4 | 92.8 | 6.2 6.3 | 6.3 | 6.3 | 1.7 1.5 | 1.6 | | 2.7 2.5 | 2.6 | |
| G2 | Sunny | Moderate | 08:35 | Surface | 1 | 25.8 25.8 | 25.8 | 6.3 6.4 | 6.4 | 33.2 33.2 | 33.2 | 97.2 97.7 | 97.5 | 6.6 6.6 | 6.6 | 6.6 | 1.8 1.8 | 1.8 | 1.8 | 5.6 5.5 | 5.6 | 5.3 |
| | | | | Middle | 5 | 25.8 25.8 | 25.8 | 6.3 6.5 | 6.4 | 33.2 33.2 | 33.2 | 96.9 97.2 | 97.1 | 6.5 6.6 | 6.6 | 6.6 | 1.8 1.7 | 1.8 | | 6.0 5.8 | 5.9 | |
| | | | | Bottom | 9 | 25.8 25.8 | 25.8 | 6.4 6.5 | 6.5 | 33.2 33.2 | 33.2 | 96.0 96.5 | 96.3 | 6.5 6.5 | 6.5 | 6.5 | 1.9 1.7 | 1.8 | | 4.5 4.5 | 4.5 | |
| G3 | Sunny | Moderate | 08:55 | Surface | 1 | 25.9 25.9 | 25.9 | 6.3 6.4 | 6.4 | 33.1 33.1 | 33.1 | 92.9 92.1 | 92.5 | 6.3 6.2 | 6.3 | 6.3 | 3.4 3.4 | 3.4 | 4.1 | 4.5 4.5 | 4.5 | 5.6 |
| | | | | Middle | 4 | 25.9 25.9 | 25.9 | 6.1 6.5 | 6.3 | 33.2 33.2 | 33.2 | 91.2 90.8 | 91.0 | 6.2 6.1 | 6.2 | 6.2 | 4.0 4.9 | 4.5 | | 7.4 7.5 | 7.5 | |
| | | | | Bottom | 7 | 25.9 25.8 | 25.9 | 6.3 6.5 | 6.4 | 33.2 33.2 | 33.2 | 89.3 89.2 | 89.3 | 6.0 6.0 | 6.0 | 6.0 | 4.5 4.5 | 4.5 | | 4.7 5.0 | 4.9 | |
| G4 | Sunny | Moderate | 09:07 | Surface | 1 | 25.7 25.7 | 25.7 | 6.5 6.5 | 6.5 | 33.1 33.1 | 33.1 | 90.9 91.5 | 91.2 | 6.2 6.2 | 6.2 | 6.2 | 2.1 2.2 | 2.2 | 2.6 | 4.9 5.0 | 5.0 | 4.9 |
| | | | | Middle | 4.5 | 25.7 25.7 | 25.7 | 6.4 6.6 | 6.5 | 33.1 33.1 | 33.1 | 90.7 91.9 | 91.3 | 6.1 6.2 | 6.2 | 6.2 | 2.2 2.3 | 2.3 | | 5.1 5.1 | 5.1 | |
| | | | | Bottom | 8 | 25.8 25.8 | 25.8 | 6.4 6.6 | 6.5 | 33.2 33.2 | 33.2 | 90.9 90.8 | 90.9 | 6.1 6.1 | 6.1 | 6.1 | 3.2 3.1 | 3.2 | | 4.7 4.7 | 4.7 | |
| M1 | Sunny | Moderate | 08:41 | Surface | 1 | 25.7 25.7 | 25.7 | 6.5 6.4 | 6.5 | 33.2 33.2 | 33.2 | 91.7 91.2 | 91.5 | 6.2 6.2 | 6.2 | 6.2 | 3.0 3.0 | 3.0 | 3.0 | 4.0 4.3 | 4.2 | 6.1 |
| | | | | Middle | 3 | 25.7 25.7 | 25.7 | 6.4 6.5 | 6.5 | 33.2 33.2 | 33.2 | 91.1 91.1 | 91.1 | 6.2 6.2 | 6.2 | 6.2 | 3.1 3.0 | 3.1 | | 9.4 9.4 | 9.4 | |
| | | | | Bottom | 5 | 25.7 25.7 | 25.7 | 6.4 6.5 | 6.5 | 33.2 33.2 | 33.2 | 90.6 90.9 | 90.8 | 6.1 6.2 | 6.2 | 6.2 | 3.0 2.8 | 2.9 | | 4.8 4.8 | 4.8 | |
| M2 | Sunny | Moderate | 08:29 | Surface | 1 | 25.8 25.8 | 25.8 | 6.0 6.2 | 6.1 | 33.2 33.3 | 33.3 | 96.6 96.8 | 96.7 | 6.5 6.5 | 6.5 | 6.5 | 2.6 2.6 | 2.6 | 2.2 | 4.6 4.6 | 4.6 | 4.7 |
| | | | | Middle | 6 | 25.8 25.8 | 25.8 | 5.9 6.3 | 6.1 | 33.3 33.3 | 33.3 | 96.0 96.0 | 96.0 | 6.5 6.5 | 6.5 | 6.5 | 2.0 1.8 | 1.9 | | 5.6 5.6 | 5.6 | |
| | | | | Bottom | 11 | 25.8 25.8 | 25.8 | 6.0 6.3 | 6.2 | 33.3 33.3 | 33.3 | 95.7 95.6 | 95.7 | 6.5 6.5 | 6.5 | 6.5 | 2.1 1.9 | 2.0 | | 3.8 3.7 | 3.8 | |
| M3 | Sunny | Moderate | 09:00 | Surface | 1 | 25.9 25.9 | 25.9 | 6.6 6.6 | 6.6 | 33.0 33.1 | 33.1 | 93.4 93.3 | 93.4 | 6.3 6.3 | 6.3 | 6.3 | 3.0 2.9 | 3.0 | 3.7 | 5.9 5.9 | 5.9 | 6.0 |
| | | | | Middle | 4 | 25.9 25.9 | 25.9 | 6.5 6.6 | 6.6 | 33.2 33.2 | 33.2 | 92.8 92.1 | 92.5 | 6.3 6.2 | 6.3 | 6.3 | 2.8 2.9 | 2.9 | | 7.1 6.9 | 7.0 | |
| | | | | Bottom | 7 | 25.8 25.8 | 25.8 | 6.6 6.6 | 6.6 | 33.2 33.2 | 33.2 | 89.4 89.7 | 89.6 | 6.0 6.1 | 6.1 | 6.1 | 5.3 5.2 | 5.3 | | 5.0 5.1 | 5.1 | |
| M4 | Sunny | Moderate | 08:22 | Surface | 1 | 25.9 25.9 | 25.9 | 6.1 6.1 | 6.1 | 33.2 33.2 | 33.2 | 96.3 95.7 | 96.0 | 6.5 6.5 | 6.5 | 6.5 | 1.6 1.7 | 1.7 | 1.7 | 5.6 5.6 | 5.6 | 4.8 |
| | | | | Middle | 5 | 25.9 25.9 | 25.9 | 6.0 6.3 | 6.2 | 33.2 33.2 | 33.2 | 95.8 95.6 | 95.7 | 6.5 6.4 | 6.5 | 6.5 | 1.7 1.7 | 1.7 | | 4.4 4.2 | 4.3 | |
| | | | | Bottom | 9 | 25.9 25.9 | 25.9 | 6.1 6.3 | 6.2 | 33.2 33.2 | 33.2 | 95.2 95.2 | 95.2 | 6.4 6.4 | 6.4 | 6.4 | 1.9 1.7 | 1.8 | | 4.4 4.4 | 4.4 | |
| M5 | Sunny | Moderate | 09:20 | Surface | 1 | 25.8 25.8 | 25.8 | 6.1 6.5 | 6.3 | 33.2 33.2 | 33.2 | 94.9 94.0 | 94.5 | 6.4 6.4 | 6.4 | 6.4 | 3.0 2.8 | 2.9 | 2.9 | 5.3 5.4 | 5.4 | 5.1 |
| | | | | Middle | 6 | 25.8 25.8 | 25.8 | 6.2 6.5 | 6.4 | 33.2 33.2 | 33.2 | 93.0 93.3 | 93.2 | 6.3 6.3 | 6.3 | 6.3 | 2.8 2.6 | 2.7 | | 5.4 5.4 | 5.4 | |
| | | | | Bottom | 11 | 25.7 25.7 | 25.7 | 6.4 6.6 | 6.5 | 33.2 33.2 | 33.2 | 92.0 92.5 | 92.3 | 6.2 6.3 | 6.3 | 6.3 | 3.3 3.1 | 3.2 | | 4.3 4.5 | 4.4 | |
| M6 | Sunny | Moderate | 09:15 | Surface | - | - | - | - | - | - | - | - | - | - | - | - | - | - | 3.2 | - | - | 4.6 |
| | | | | Middle | 2.1 | 25.7 25.7 | 25.7 | 6.3 6.2 | 6.3 | 33.2 33.2 | 33.2 | 89.2 88.9 | 89.1 | 6.0 6.0 | 6.0 | 6.0 | 2.9 3.5 | 3.2 | | 4.7 4.5 | 4.6 | |
| | | | | Bottom | - | - | - | - | - | - | - | - | - | - | - | - | - | - | | - | - | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 30 October 2017 (Mid-Ebb Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 5.6 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 6.1 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.8 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.8 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.6 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.1 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 30 October 2017**

(Mid-Flood Tide)

| Location | Weather Condition | Sea Condition** | Sampling Time | Depth (m) | | Temperature (°C) | | pH | | Salinity ppt | | DO Saturation (%) | | Dissolved Oxygen (mg/L) | | | Turbidity(NTU) | | | Suspended Solids (mg/L) | | |
|----------|-------------------|-----------------|---------------|-----------|------|------------------|---------|-------|---------|--------------|---------|-------------------|---------|-------------------------|---------|-----|----------------|---------|-----|-------------------------|---------|-----|
| | | | | | | Value | Average | Value | Average | Value | Average | Value | Average | Value | Average | DA* | Value | Average | DA* | Value | Average | DA* |
| C1 | Sunny | Moderate | 16:10 | Surface | 1 | 25.9 | 25.9 | 6.9 | 7.0 | 33.3 | 33.3 | 109.9 | 109.9 | 7.4 | 7.4 | 7.2 | 1.2 | 1.3 | 3.4 | 4.6 | 4.4 | 4.5 |
| | | | | | 25.8 | 25.8 | 6.7 | 6.9 | 33.3 | 33.3 | 101.9 | 102.3 | 6.9 | 6.9 | 2.0 | | 2.2 | 6.5 | | 6.3 | 6.4 | |
| | | | | | 25.8 | 25.8 | 7.0 | 7.1 | 33.3 | 33.3 | 97.3 | 102.6 | 6.6 | 6.9 | 6.7 | | 6.7 | 4.6 | | 4.6 | 4.6 | |
| C2 | Sunny | Moderate | 14:39 | Surface | 1 | 26.1 | 26.1 | 8.8 | 8.2 | 33.4 | 33.1 | 105.0 | 105.4 | 7.1 | 7.1 | 6.7 | 1.4 | 1.4 | 3.4 | 4.2 | 4.1 | 4.2 |
| | | | | | 26.1 | 26.0 | 7.6 | 7.7 | 33.2 | 33.2 | 105.7 | 94.0 | 6.3 | 6.3 | 2.1 | | 2.0 | 2.6 | | 2.6 | | |
| | | | | | 26.0 | 26.0 | 7.5 | 7.6 | 33.2 | 33.2 | 93.8 | 91.2 | 6.3 | 6.2 | 1.9 | | 6.7 | 3.5 | | 3.5 | 3.5 | |
| G1 | Sunny | Moderate | 15:27 | Surface | 1 | 25.9 | 25.9 | 6.8 | 6.9 | 33.1 | 33.1 | 103.8 | 104.0 | 7.0 | 7.0 | 6.9 | 2.6 | 2.6 | 2.9 | 4.3 | 4.1 | 4.2 |
| | | | | | 25.9 | 25.8 | 7.0 | 7.0 | 33.0 | 33.2 | 104.1 | 98.7 | 6.7 | 6.7 | 3.0 | | 3.4 | 7.5 | | 7.5 | | |
| | | | | | 25.8 | 25.8 | 7.1 | 7.1 | 33.2 | 33.2 | 99.7 | 97.3 | 6.7 | 6.6 | 3.7 | | 2.5 | 3.7 | | 3.7 | | |
| G2 | Sunny | Moderate | 15:13 | Surface | 1 | 26.0 | 26.0 | 7.0 | 7.1 | 33.1 | 33.1 | 109.1 | 109.1 | 7.4 | 7.4 | 7.3 | 1.8 | 1.8 | 1.7 | 4.3 | 4.2 | 4.3 |
| | | | | | 26.0 | 25.9 | 7.2 | 7.2 | 33.1 | 33.3 | 109.1 | 107.0 | 6.8 | 7.2 | 1.5 | | 1.6 | 4.0 | | 3.8 | | |
| | | | | | 25.9 | 25.9 | 7.2 | 7.2 | 33.3 | 33.3 | 106.4 | 102.6 | 6.6 | 7.0 | 1.6 | | 1.6 | 3.6 | | 3.5 | | |
| G3 | Sunny | Moderate | 15:36 | Surface | 1 | 25.8 | 25.8 | 6.8 | 6.9 | 32.6 | 32.7 | 96.0 | 96.0 | 6.5 | 6.5 | 6.5 | 4.2 | 4.5 | 6.3 | 4.5 | 4.5 | 4.5 |
| | | | | | 25.8 | 25.8 | 7.0 | 7.0 | 32.8 | 33.0 | 96.0 | 95.0 | 6.5 | 6.5 | 4.8 | | 7.0 | 4.5 | | 6.6 | | |
| | | | | | 25.8 | 25.8 | 6.9 | 7.0 | 32.9 | 33.2 | 95.7 | 93.1 | 6.4 | 6.4 | 6.6 | | 7.4 | 4.5 | | 4.5 | | |
| G4 | Sunny | Moderate | 15:49 | Surface | 1 | 26.0 | 26.1 | 7.1 | 7.0 | 33.1 | 33.1 | 101.1 | 101.4 | 6.8 | 6.8 | 6.8 | 2.4 | 2.5 | 3.1 | 5.1 | 4.9 | 5.0 |
| | | | | | 26.1 | 25.8 | 6.9 | 7.0 | 33.1 | 33.2 | 101.6 | 101.2 | 6.8 | 6.7 | 2.6 | | 2.6 | 5.9 | | 6.0 | | |
| | | | | | 25.8 | 25.8 | 7.0 | 7.0 | 33.2 | 33.2 | 97.2 | 96.8 | 6.6 | 6.5 | 4.0 | | 4.1 | 5.2 | | 5.2 | | |
| M1 | Sunny | Moderate | 15:20 | Surface | 1 | 25.9 | 25.9 | 7.2 | 7.1 | 33.2 | 33.2 | 104.8 | 105.3 | 7.1 | 7.1 | 7.0 | 2.5 | 2.4 | 3.4 | 3.5 | 3.4 | 3.5 |
| | | | | | 25.9 | 25.8 | 7.0 | 7.1 | 33.2 | 33.2 | 105.7 | 100.5 | 6.8 | 6.8 | 3.0 | | 3.1 | 5.9 | | 5.9 | | |
| | | | | | 25.8 | 25.8 | 7.1 | 7.1 | 33.2 | 33.2 | 98.7 | 97.0 | 6.7 | 6.6 | 3.2 | | 4.2 | 3.6 | | 3.6 | | |
| M2 | Sunny | Moderate | 15:03 | Surface | 1 | 26.0 | 26.0 | 6.7 | 7.0 | 33.1 | 33.2 | 110.0 | 110.5 | 7.4 | 7.5 | 7.4 | 1.5 | 1.6 | 1.6 | 3.8 | 4.0 | 3.9 |
| | | | | | 26.0 | 25.9 | 7.2 | 7.1 | 33.2 | 33.3 | 111.0 | 106.7 | 7.5 | 7.2 | 1.6 | | 1.1 | 3.6 | | 3.4 | | |
| | | | | | 25.9 | 25.9 | 7.2 | 7.2 | 33.3 | 33.3 | 107.8 | 100.9 | 6.6 | 6.8 | 1.1 | | 1.9 | 2.7 | | 2.8 | | |
| M3 | Sunny | Moderate | 15:42 | Surface | 1 | 25.9 | 25.9 | 7.2 | 7.2 | 32.5 | 32.8 | 96.6 | 96.8 | 6.5 | 6.5 | 6.5 | 3.5 | 3.5 | 3.8 | 4.5 | 4.5 | 4.5 |
| | | | | | 25.9 | 25.8 | 7.1 | 7.1 | 33.0 | 33.1 | 96.9 | 94.3 | 6.5 | 6.4 | 3.5 | | 4.2 | 4.5 | | 9.6 | | |
| | | | | | 25.8 | 25.8 | 7.1 | 7.2 | 33.1 | 33.1 | 94.3 | 94.0 | 6.4 | 6.4 | 4.4 | | 3.7 | 9.4 | | 3.7 | | |
| M4 | Sunny | Moderate | 14:49 | Surface | 1 | 26.0 | 26.0 | 7.2 | 7.3 | 33.2 | 33.2 | 111.8 | 112.2 | 7.5 | 7.6 | 7.6 | 1.7 | 1.7 | 1.7 | 4.9 | 4.7 | 4.8 |
| | | | | | 26.0 | 26.0 | 7.4 | 7.4 | 33.2 | 33.3 | 112.6 | 111.2 | 7.6 | 7.5 | 1.6 | | 1.6 | 4.7 | | 3.6 | | |
| | | | | | 26.0 | 26.0 | 7.3 | 7.4 | 33.3 | 33.3 | 110.1 | 112.2 | 7.4 | 7.5 | 1.7 | | 1.4 | 3.6 | | 3.5 | | |
| M5 | Sunny | Moderate | 16:02 | Surface | 1 | 26.0 | 26.0 | 6.5 | 6.6 | 33.2 | 33.2 | 113.8 | 112.1 | 7.7 | 7.6 | 7.1 | 1.7 | 1.8 | 2.8 | 4.6 | 4.6 | 4.6 |
| | | | | | 25.9 | 25.8 | 6.7 | 6.7 | 33.2 | 33.3 | 110.3 | 98.1 | 7.4 | 6.6 | 1.8 | | 3.8 | 4.6 | | 6.7 | | |
| | | | | | 25.8 | 25.8 | 6.4 | 6.6 | 33.3 | 33.3 | 98.1 | 99.0 | 6.6 | 6.7 | 3.4 | | 2.9 | 6.6 | | 6.6 | | |
| M6 | Sunny | Moderate | 15:56 | Surface | - | - | - | - | - | - | - | - | - | - | 6.6 | - | - | 2.9 | - | - | - | |
| | | | | | 2.1 | 25.8 | 25.8 | 7.0 | 7.0 | 33.2 | 33.2 | 97.0 | 96.9 | 6.6 | | 6.6 | 2.9 | | 2.9 | 7.1 | 6.8 | |
| | | | | | - | 25.8 | 25.8 | 6.9 | 7.0 | 33.2 | 33.2 | 96.7 | - | 6.5 | | 6.6 | 2.9 | | - | 6.8 | 7.0 | |

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.


Appendix I - Action and Limit Levels for Marine Water Quality on 30 October (Mid-Flood Tide)

| Parameter (unit) | Depth | Action Level | Limit Level |
|---|-------------------------------------|---|---|
| DO in mg/L (See Note 1 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Depth Average | <u>4.9 mg/L</u> | <u>4.6 mg/L</u> |
| | Bottom | <u>4.2 mg/L</u> | <u>3.6 mg/L</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>5.0 mg/L</u> | <u>4.7 mg/L</u> |
| Turbidity in NTU (See Note 2 and 4) | <u>Stations G1-G4, M1-M5</u> | | |
| | Bottom | <u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 8.0 NTU</u> | <u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 8.7 NTU</u> |
| | <u>Station M6</u> | | |
| | Intake Level | <u>19.0 NTU</u> | <u>19.4 NTU</u> |
| | SS in mg/L (See Note 2 and 4) | <u>Stations G1-G4</u> | |
| Surface | | <u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.4 mg/L</u> | <u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> |
| <u>Stations M1-M5</u> | | | |
| Surface | | <u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.4 mg/L</u> | <u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u> |
| <u>Stations G1-G4, M1-M5</u> | | | |
| Bottom | | <u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.5 mg/L</u> | <u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.0 mg/L</u> |
| <u>Station M6</u> | | | |
| Intake Level | <u>8.3 mg/L</u> | <u>8.6 mg/L</u> | |

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Dissolved Oxygen (Depth-averaged) at Mid-Ebb Tide

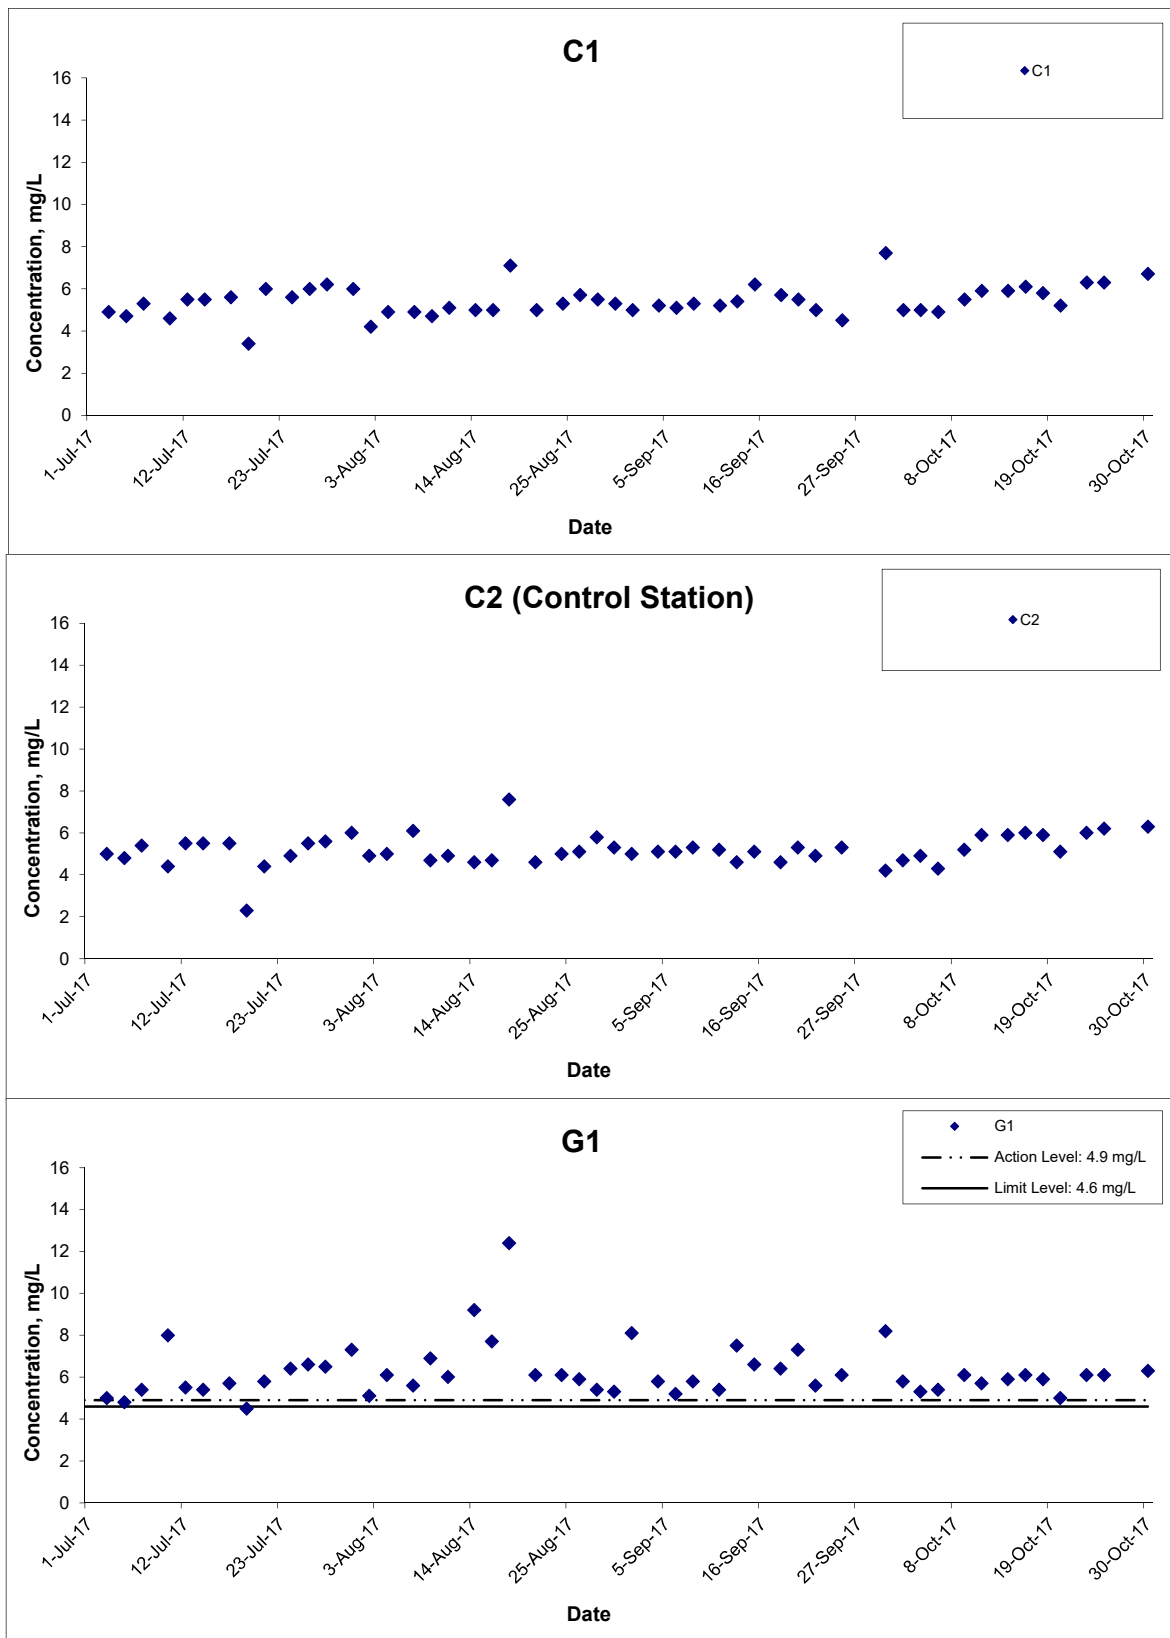

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Dissolved Oxygen (Depth-averaged) at Mid-Ebb Tide

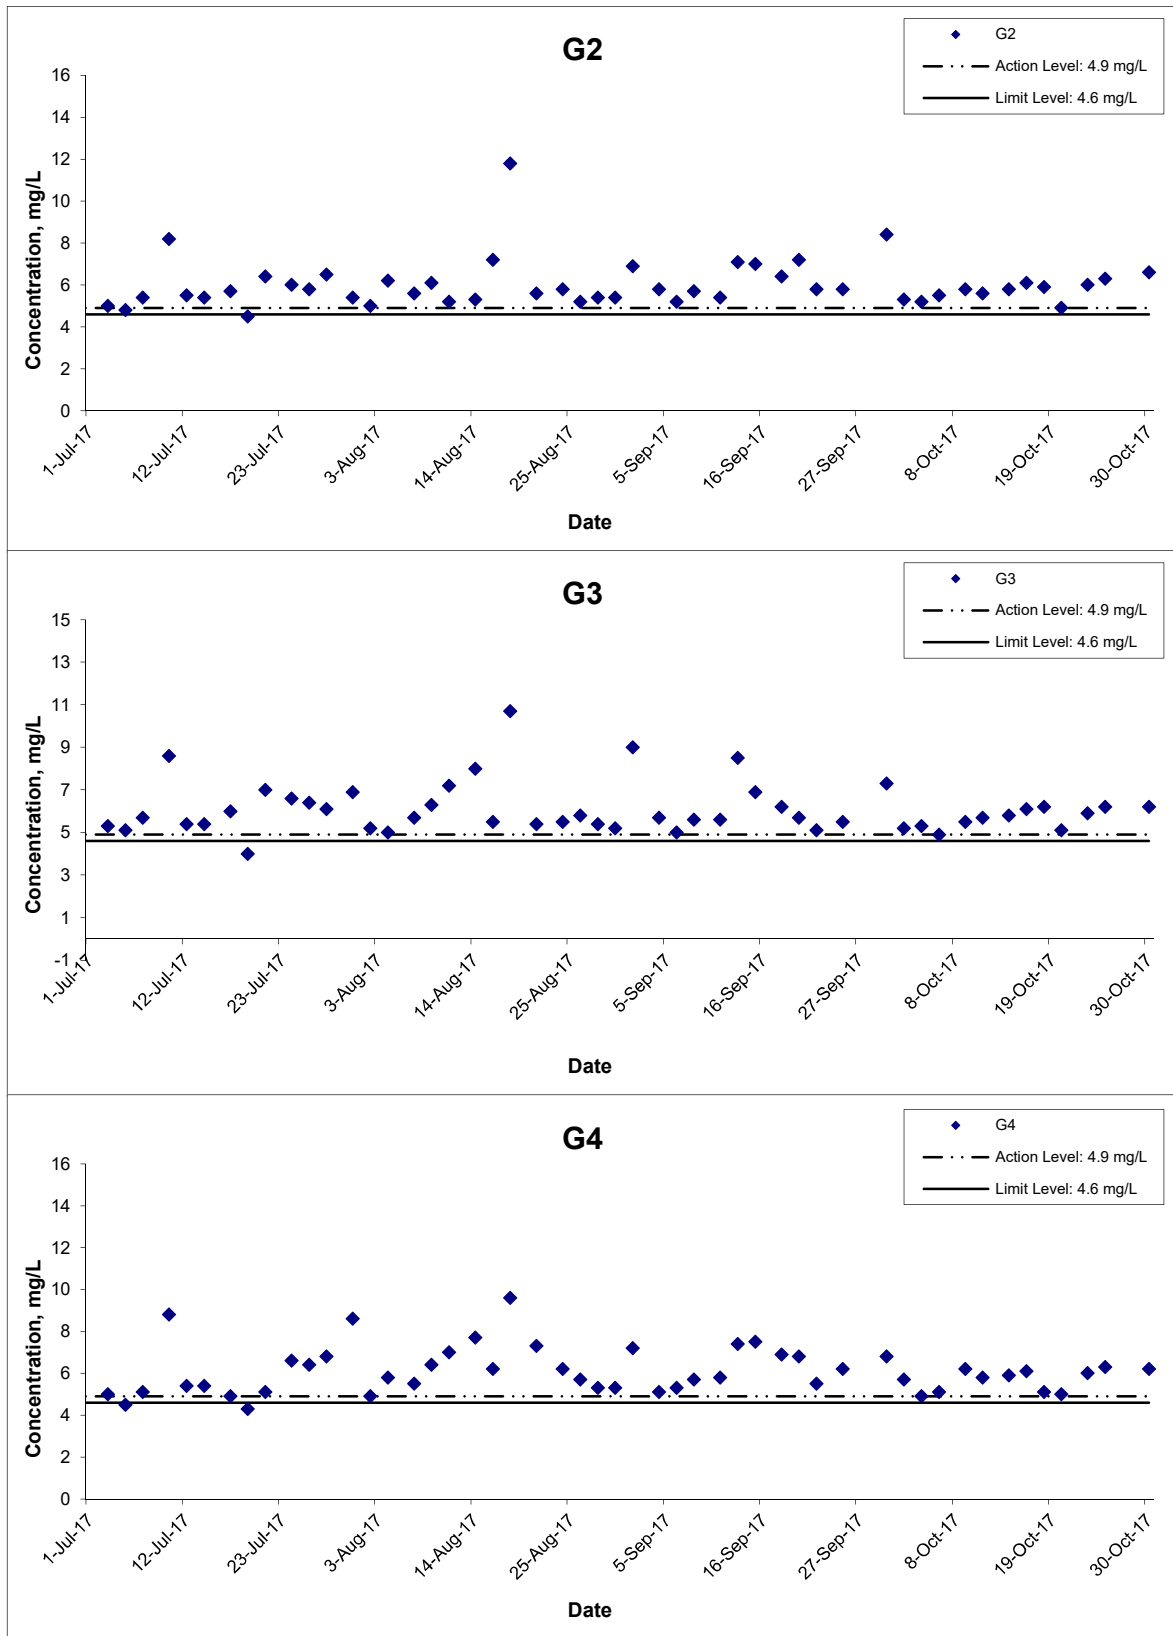


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I



Dissolved Oxygen (Depth-averaged) at Mid-Ebb Tide

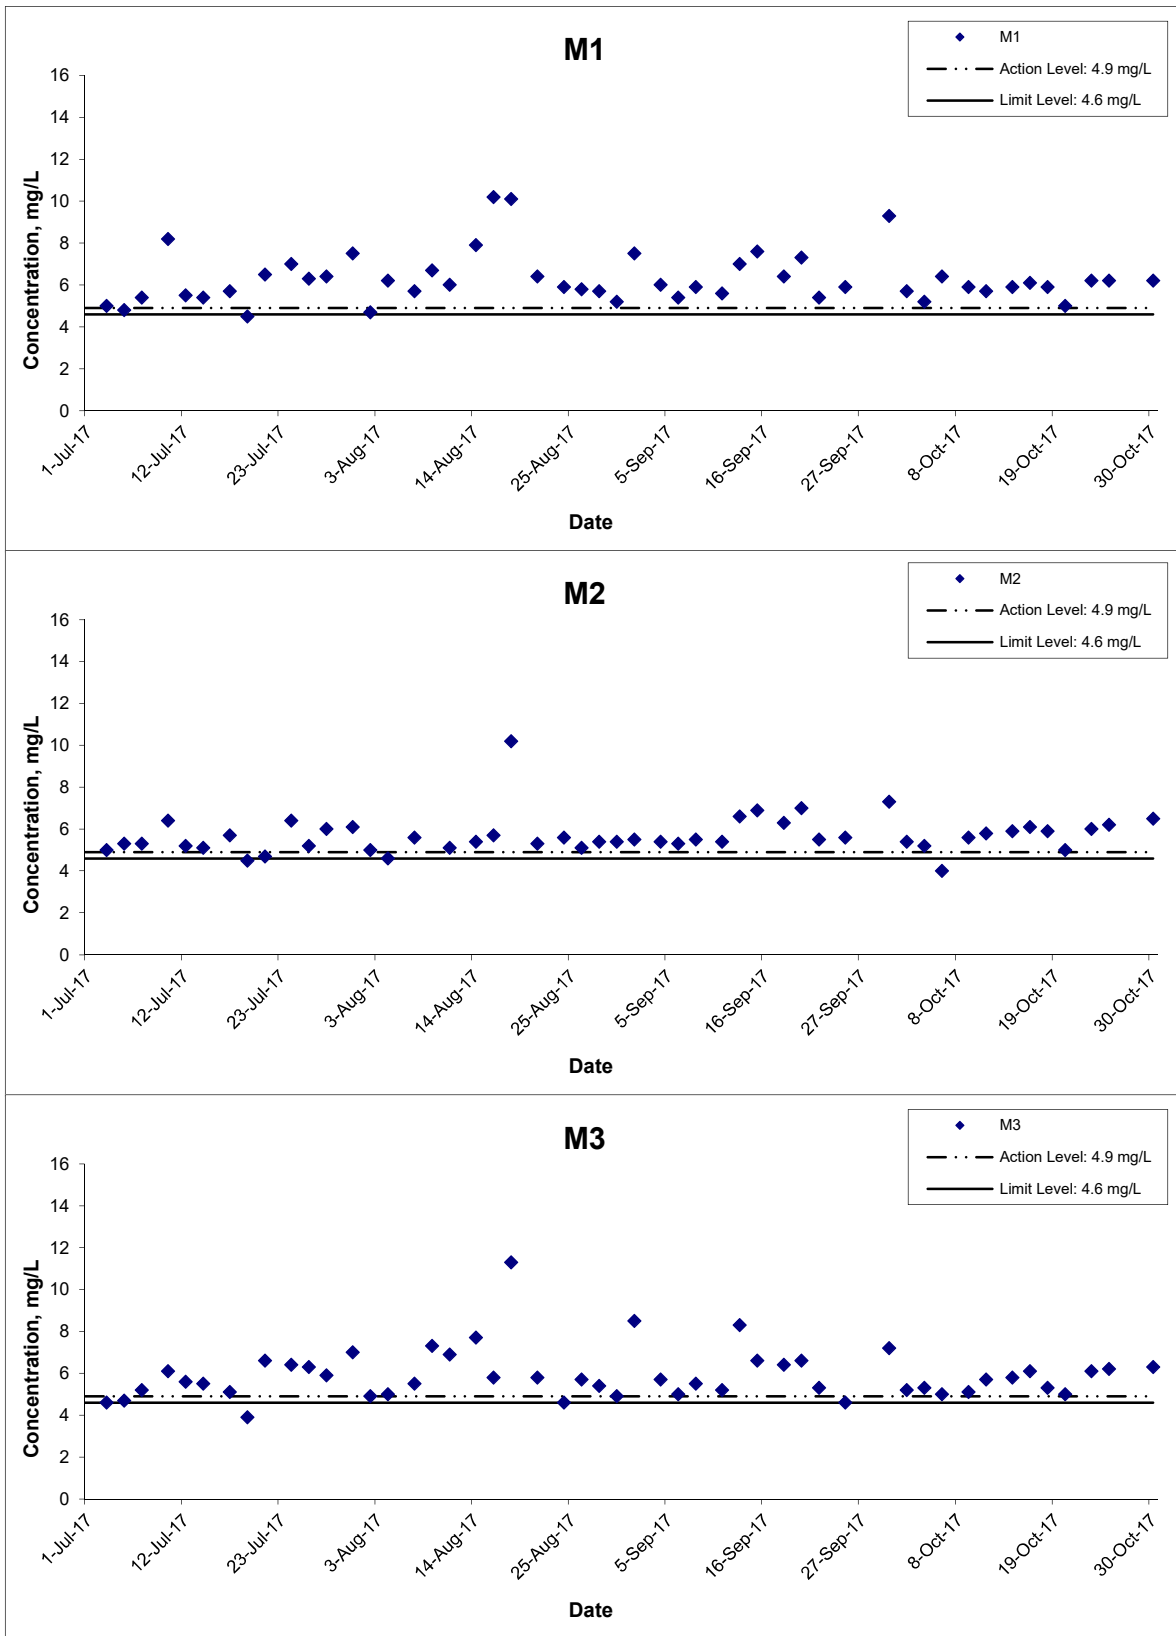


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I




Dissolved Oxygen (Depth-averaged) at Mid-Ebb Tide

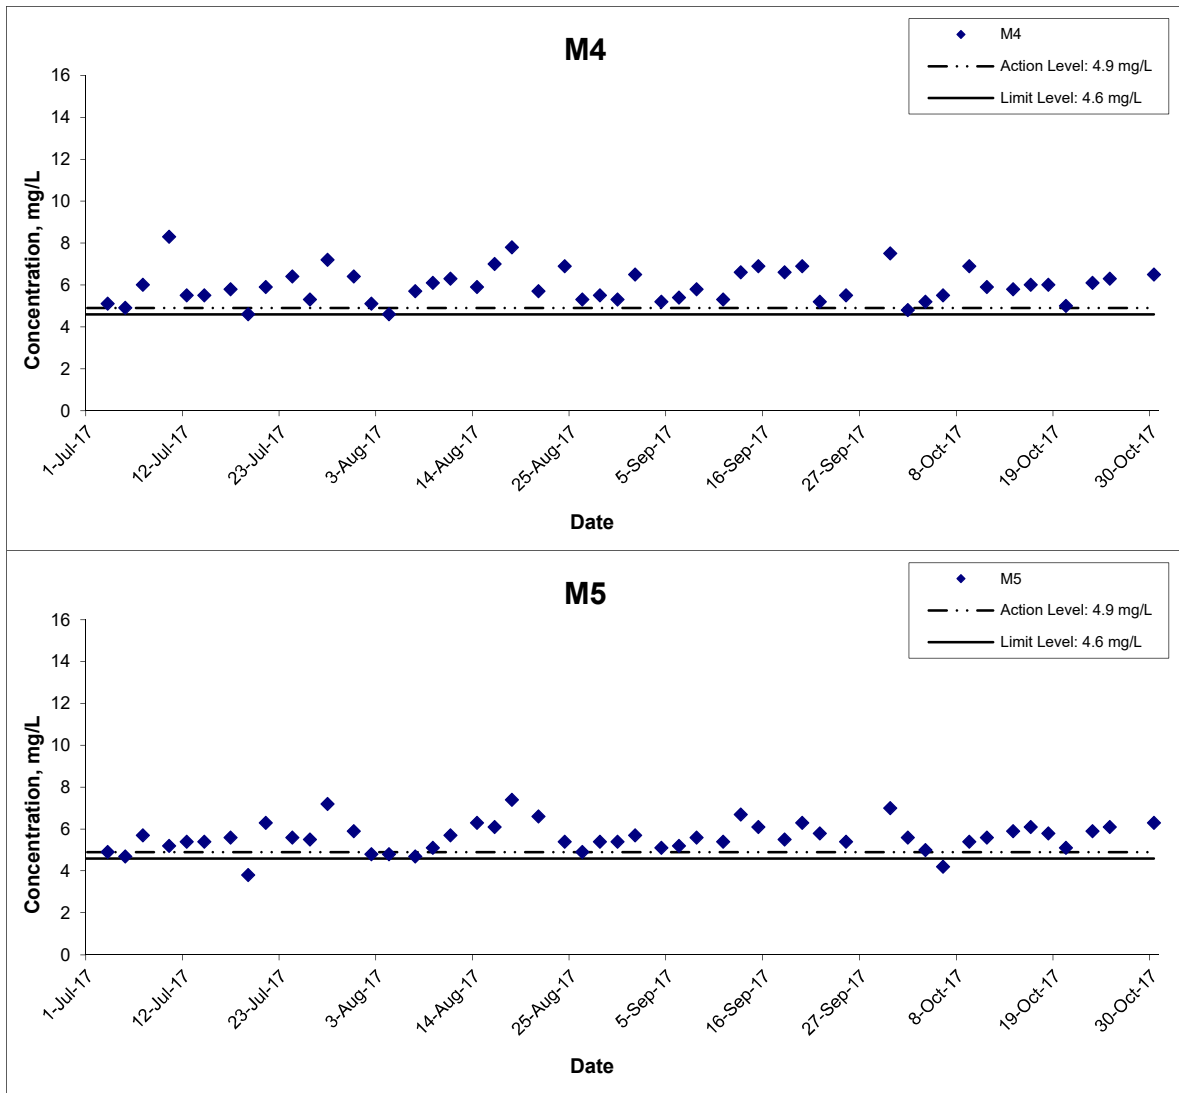

| | | | | | | |
|-------|--|-------|--------|-------------|---------|-----------------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Water Quality Monitoring Results | Date | Oct 17 | Appendix | I | |

Dissolved Oxygen (Depth-averaged) at Mid-Flood Tide

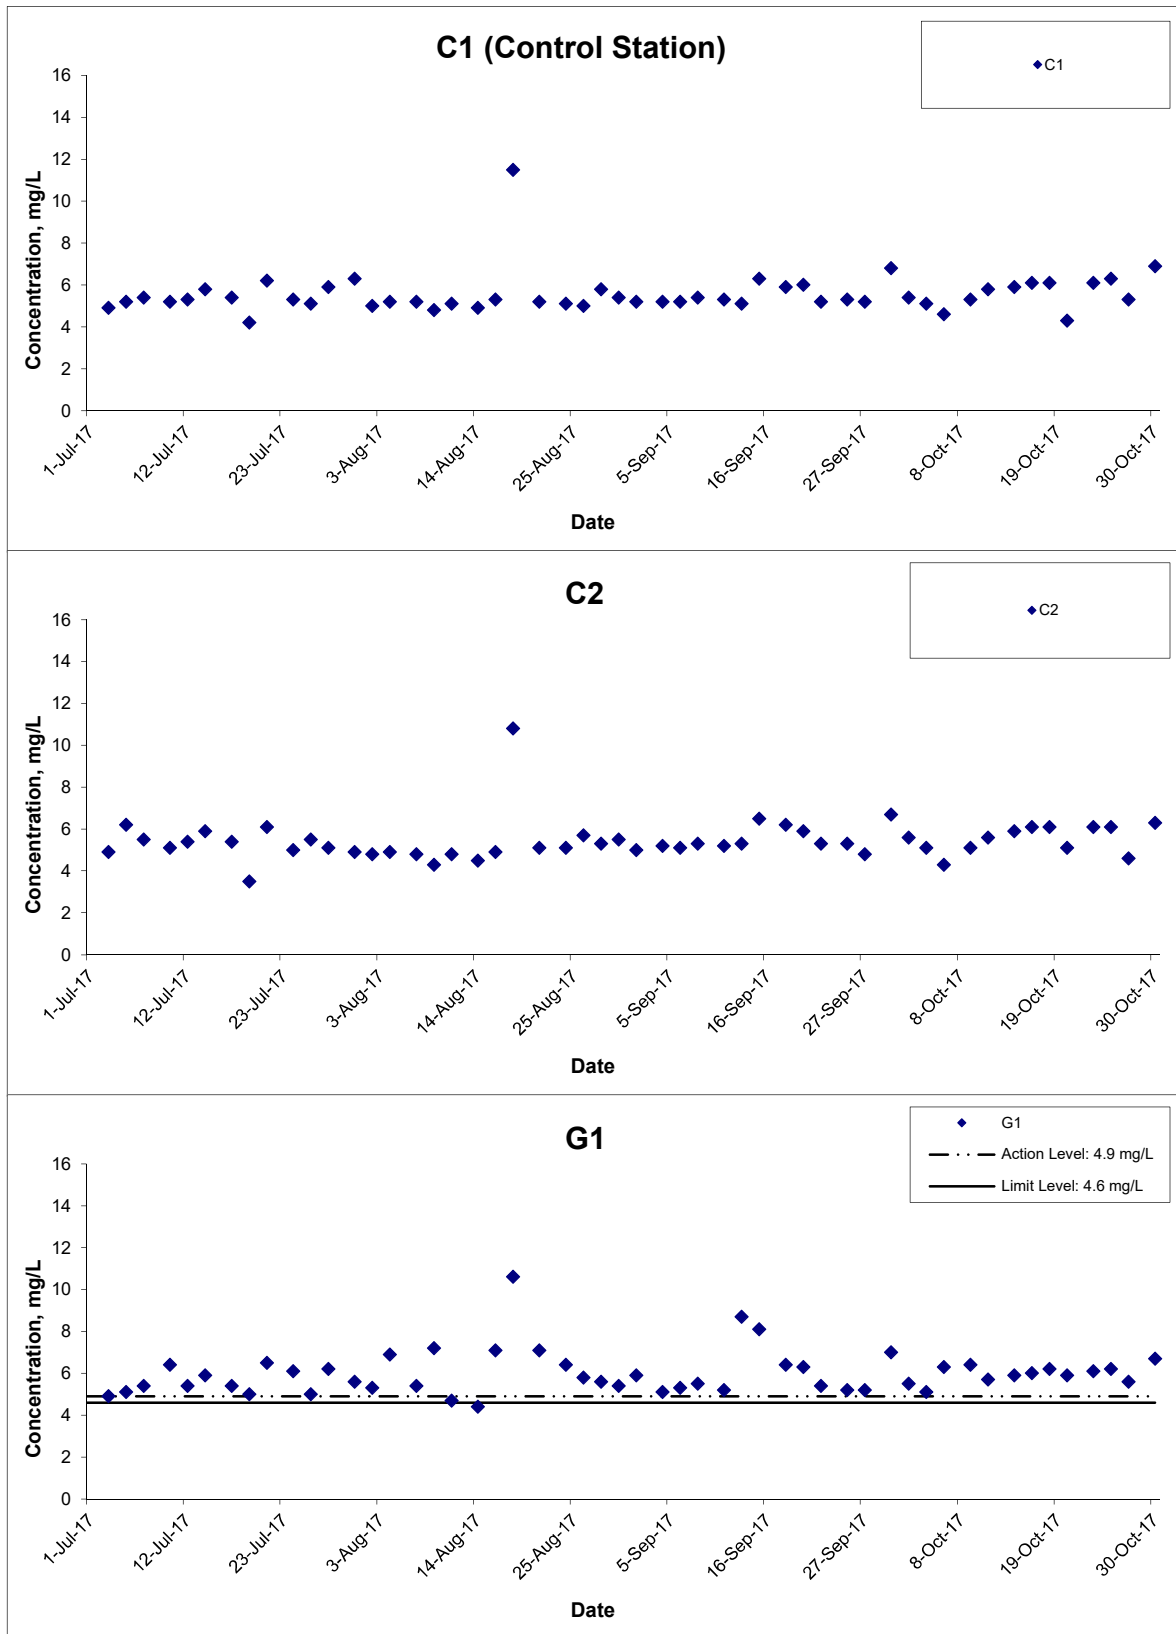


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I



Dissolved Oxygen (Depth-averaged) at Mid-Flood Tide

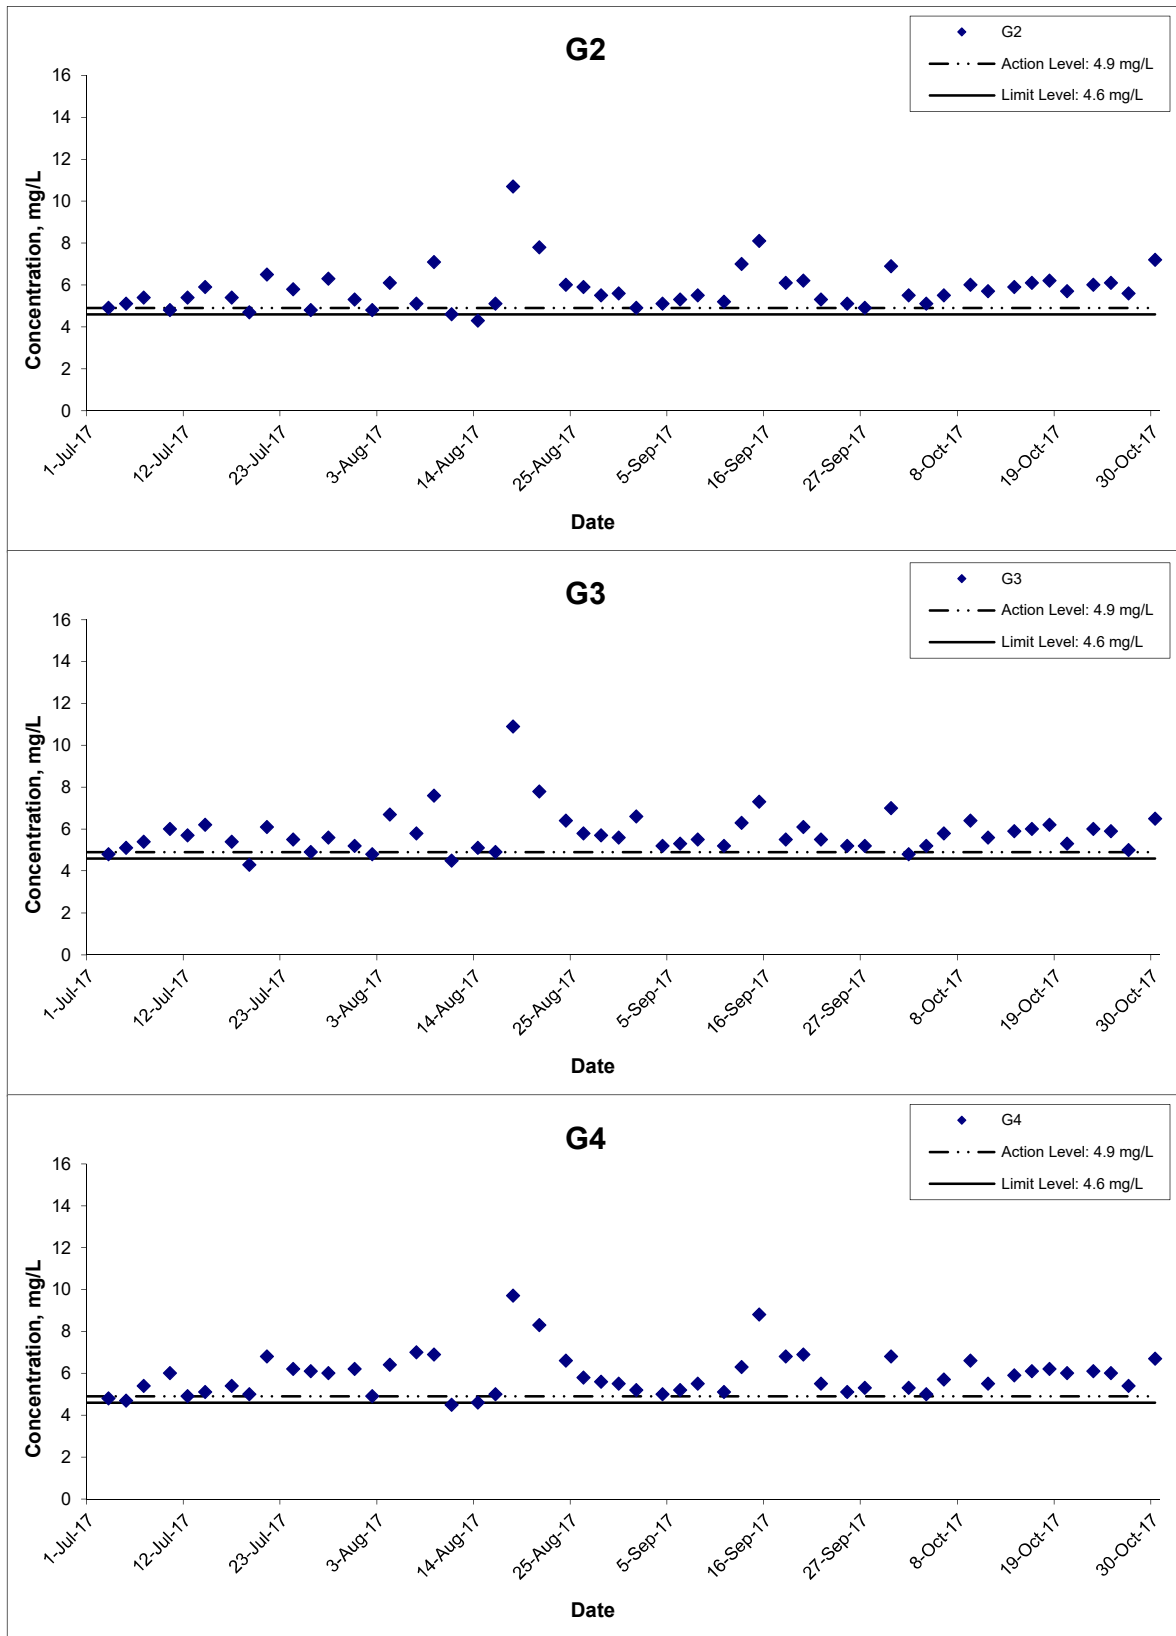

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Dissolved Oxygen (Depth-averaged) at Mid-Flood Tide

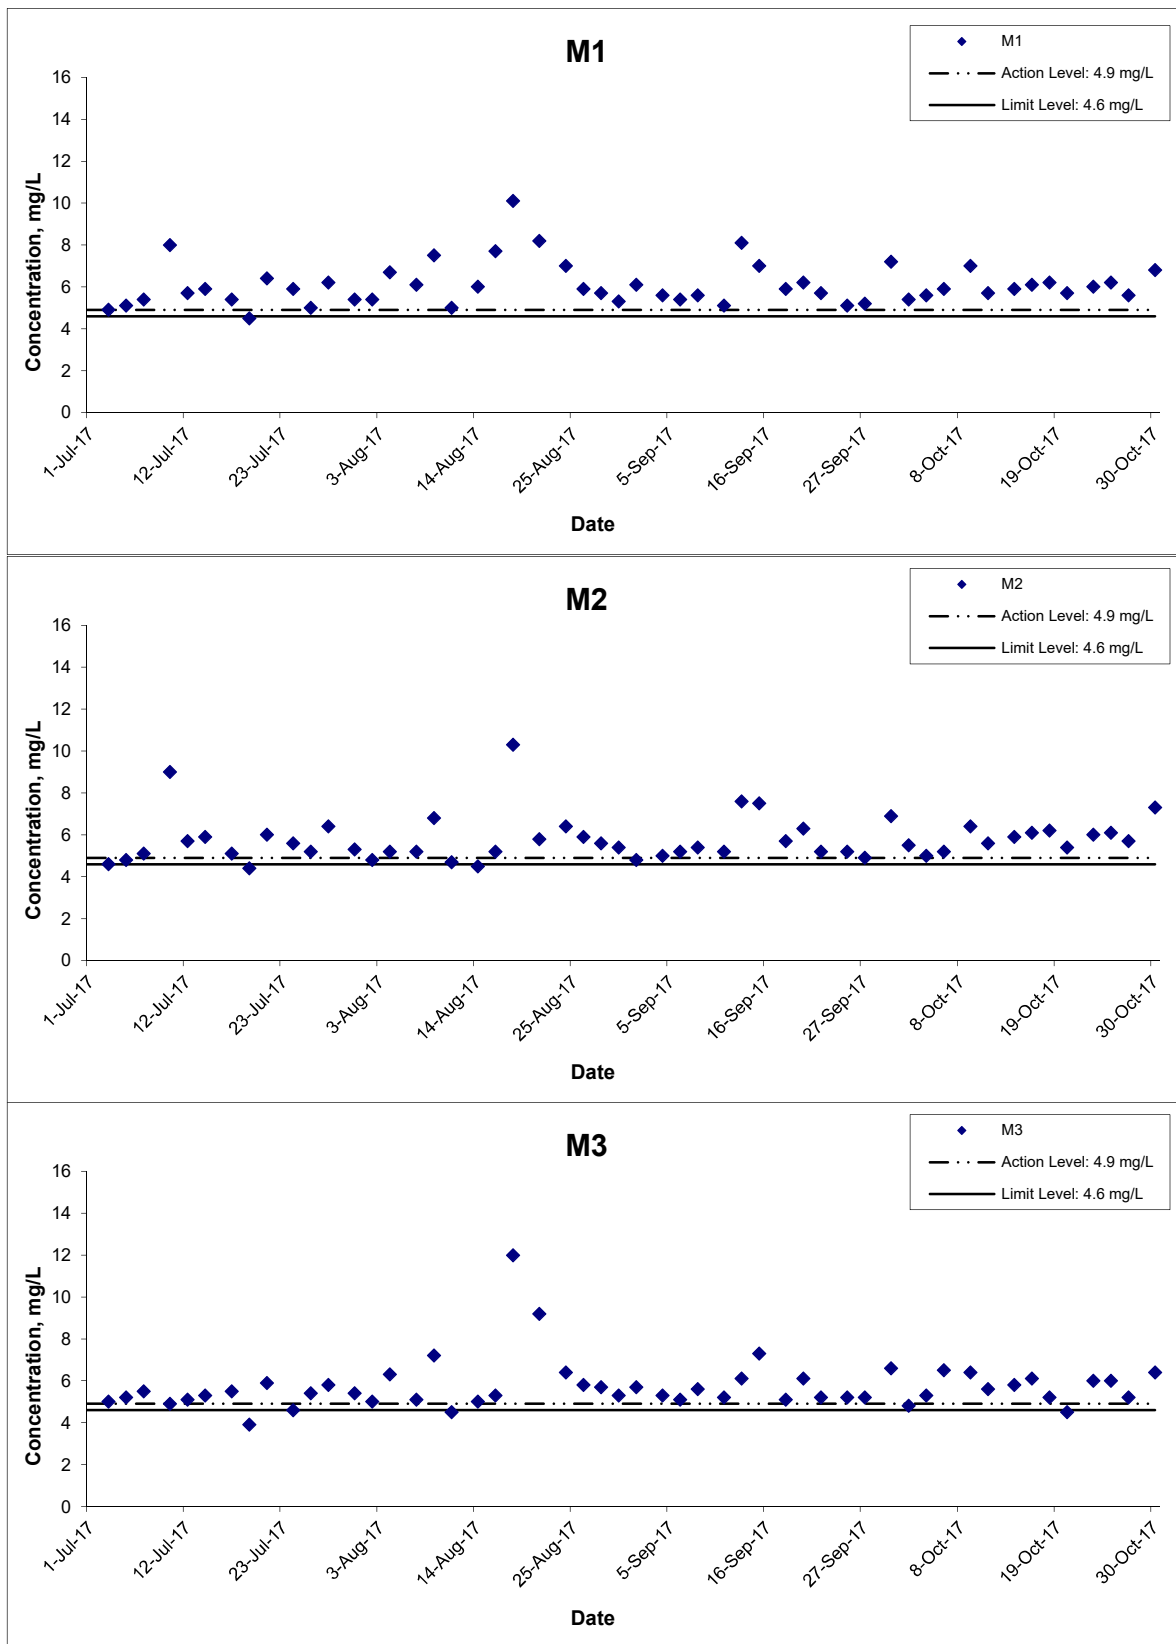


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I






Dissolved Oxygen (Depth-averaged) at Mid-Flood Tide

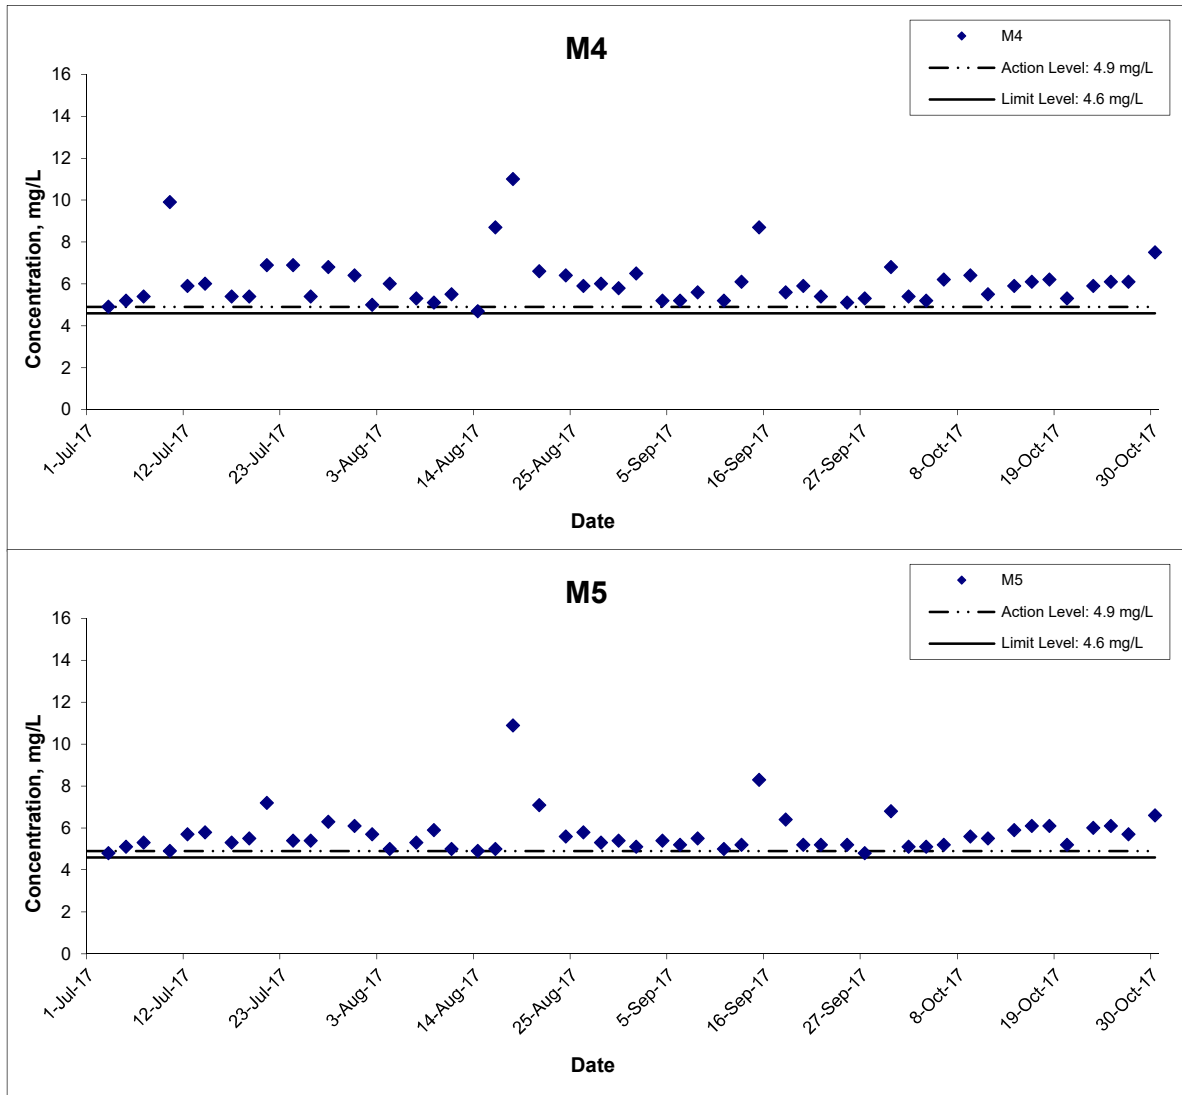

| | | | | | | |
|-------|--|-------|--------|-------------|---------|-----------------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Water Quality Monitoring Results | Date | Oct 17 | Appendix | I | |

Dissolved Oxygen (Bottom) at Mid-Ebb Tide

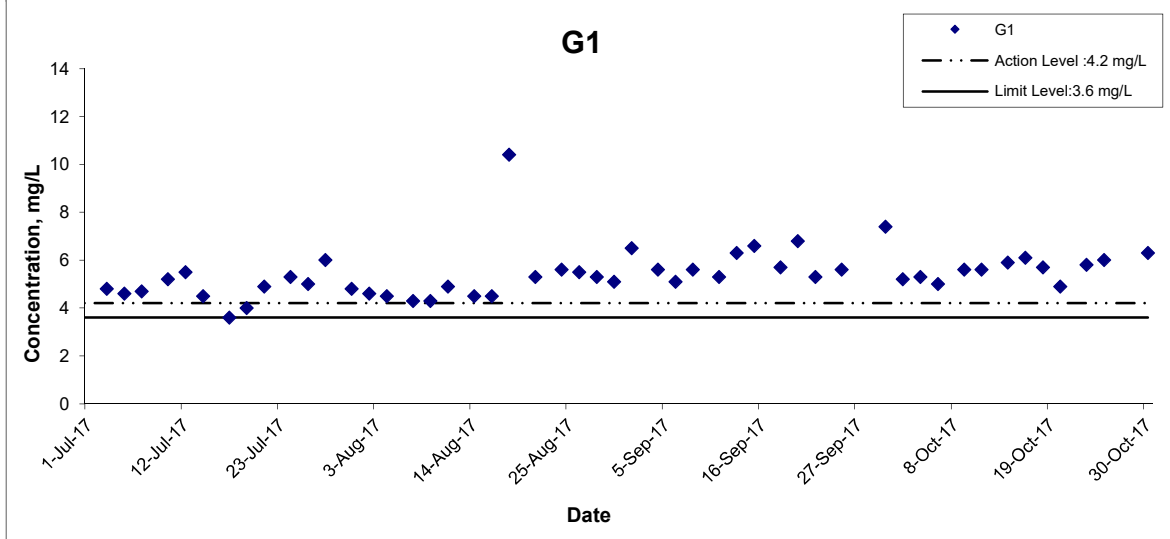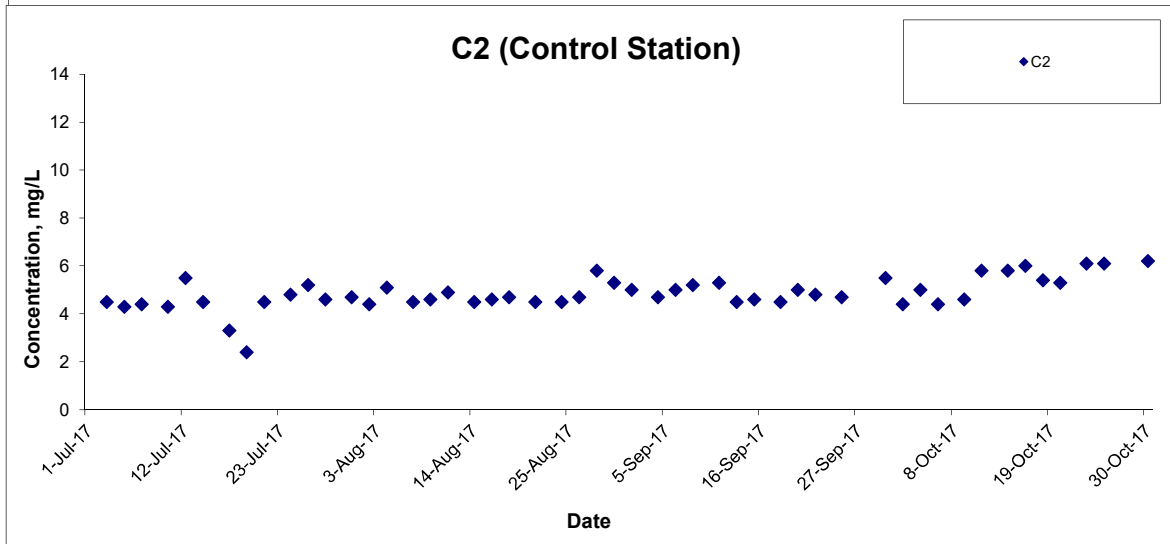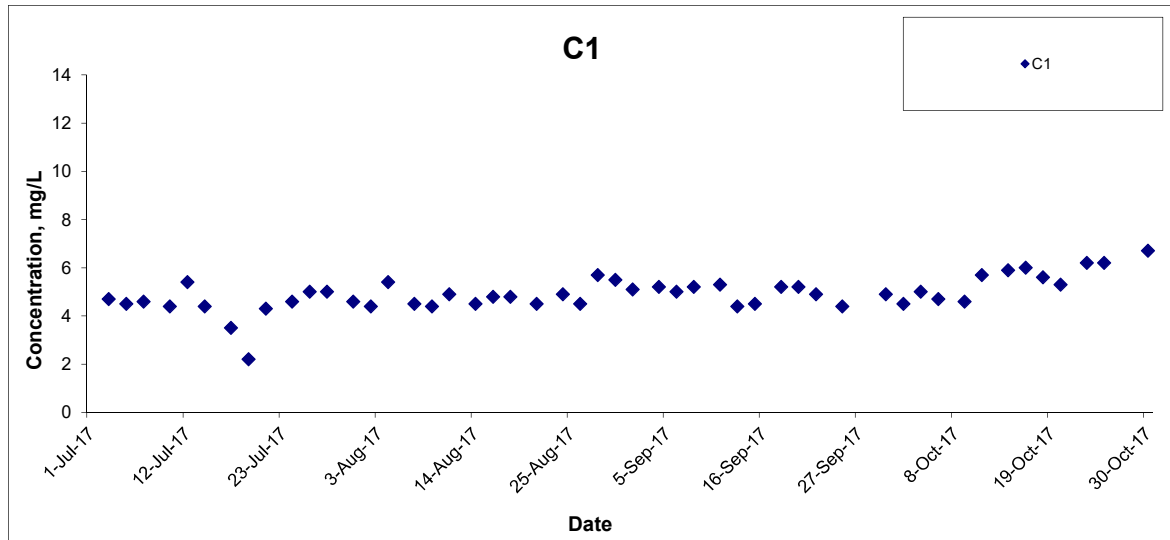


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I



Dissolved Oxygen (Bottom) at Mid-Ebb Tide

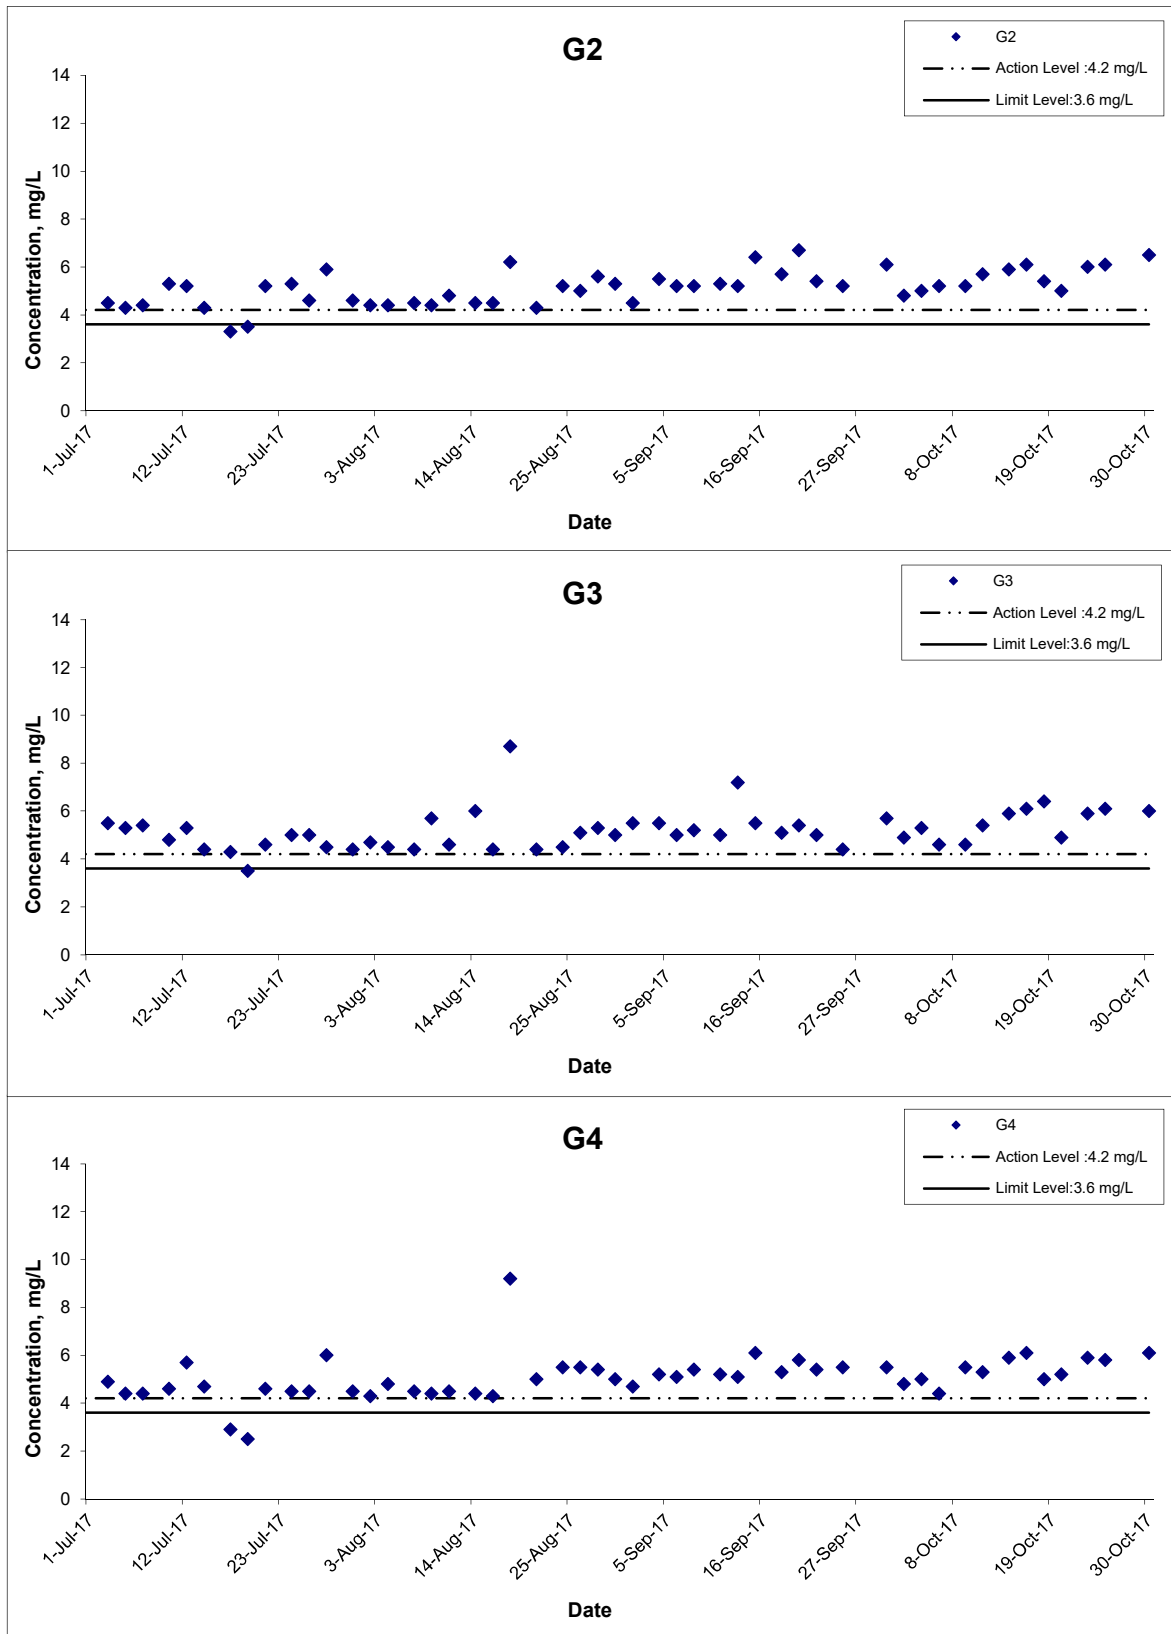


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I



Dissolved Oxygen (Bottom) at Mid-Ebb Tide

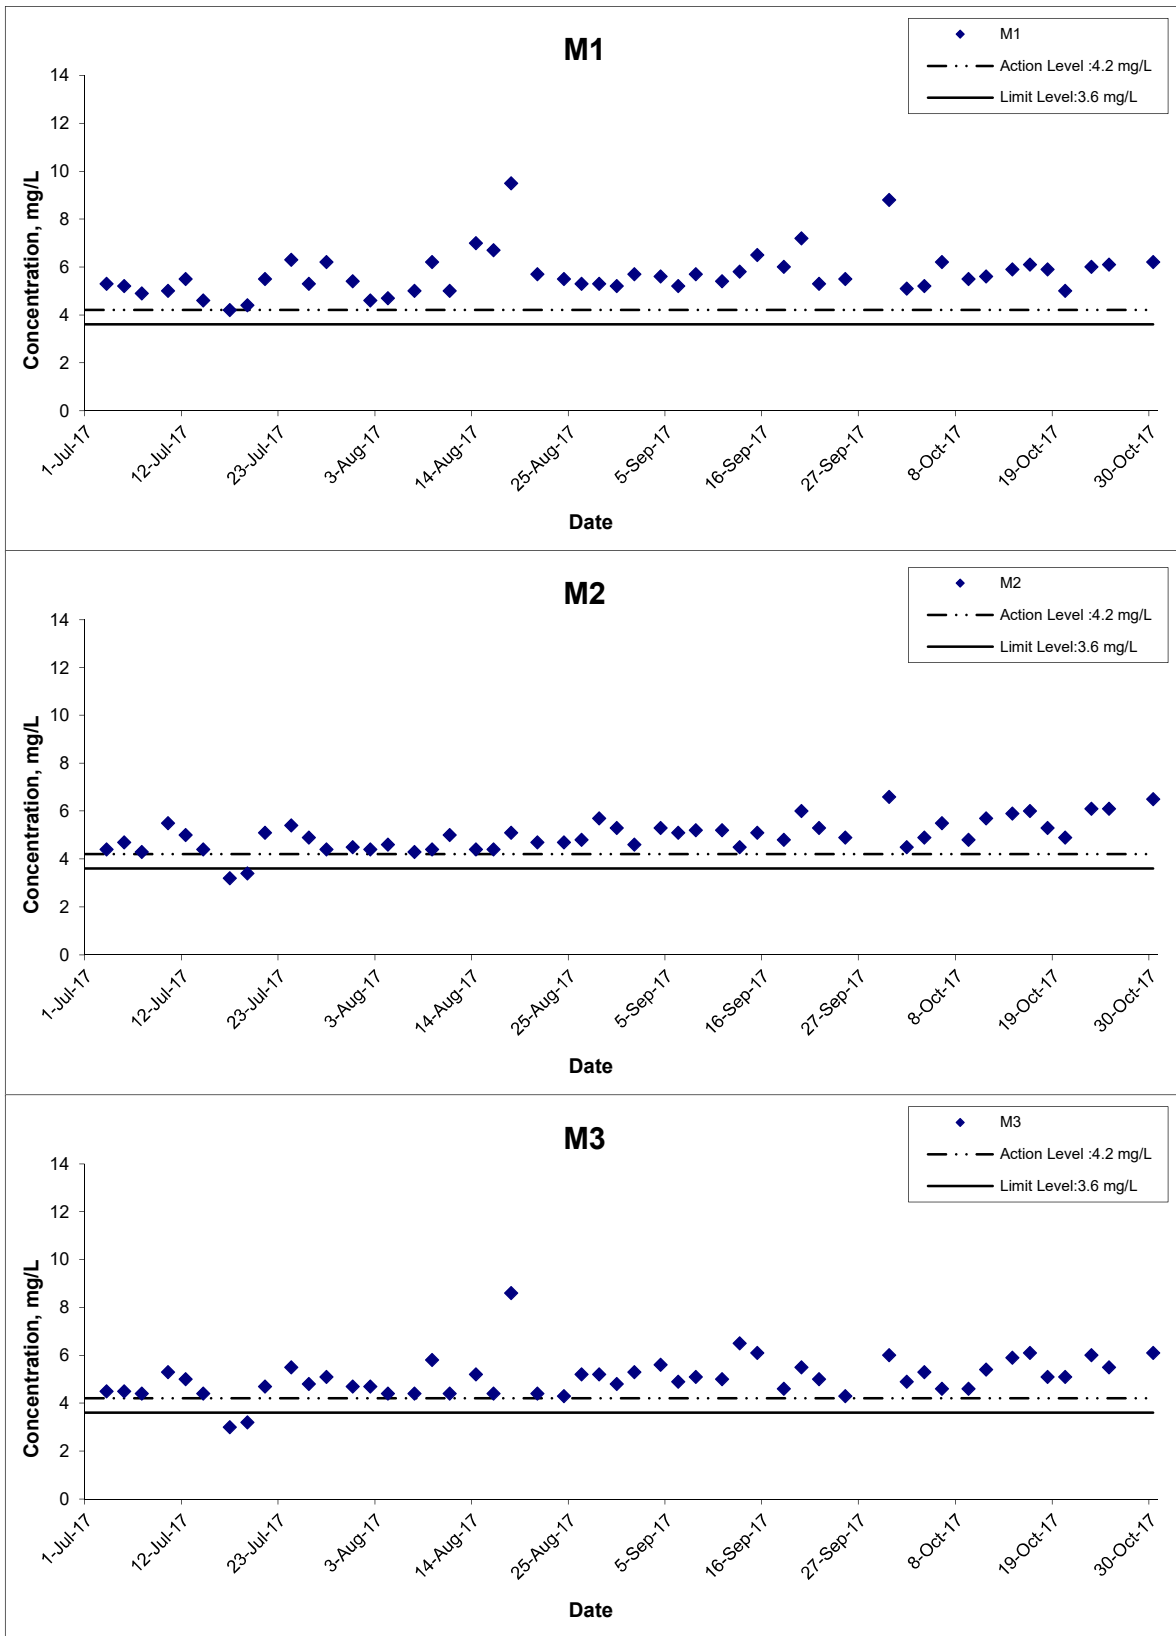


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I




Dissolved Oxygen (Bottom) at Mid-Ebb Tide

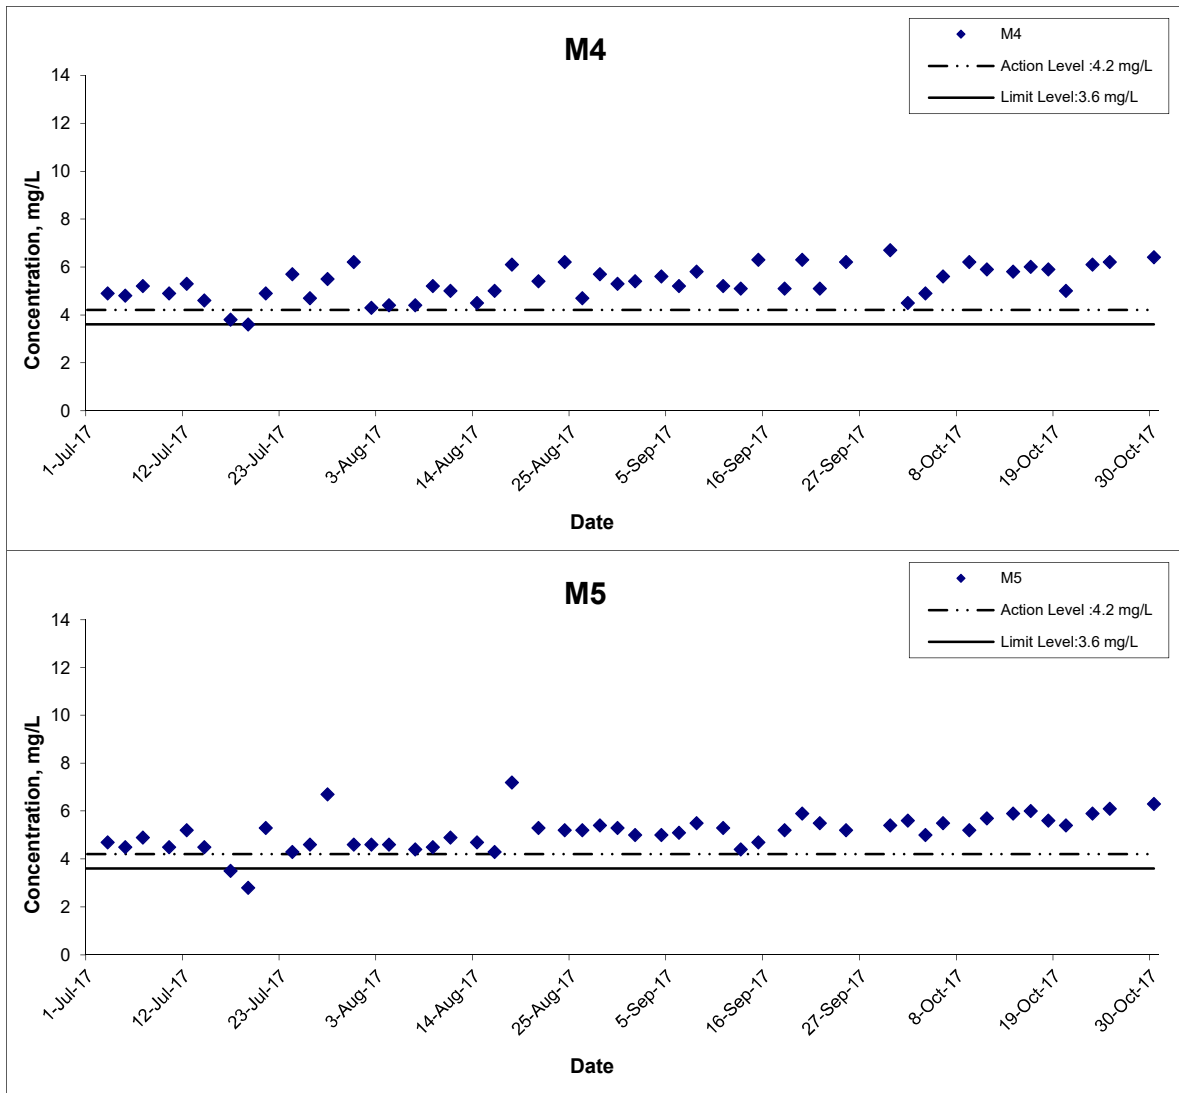

| | | | | | | |
|-------|--|-------|--------|-------------|---------|-----------------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Water Quality Monitoring Results | Date | Oct 17 | Appendix | I | |

Dissolved Oxygen (Bottom) at Mid-Flood Tide

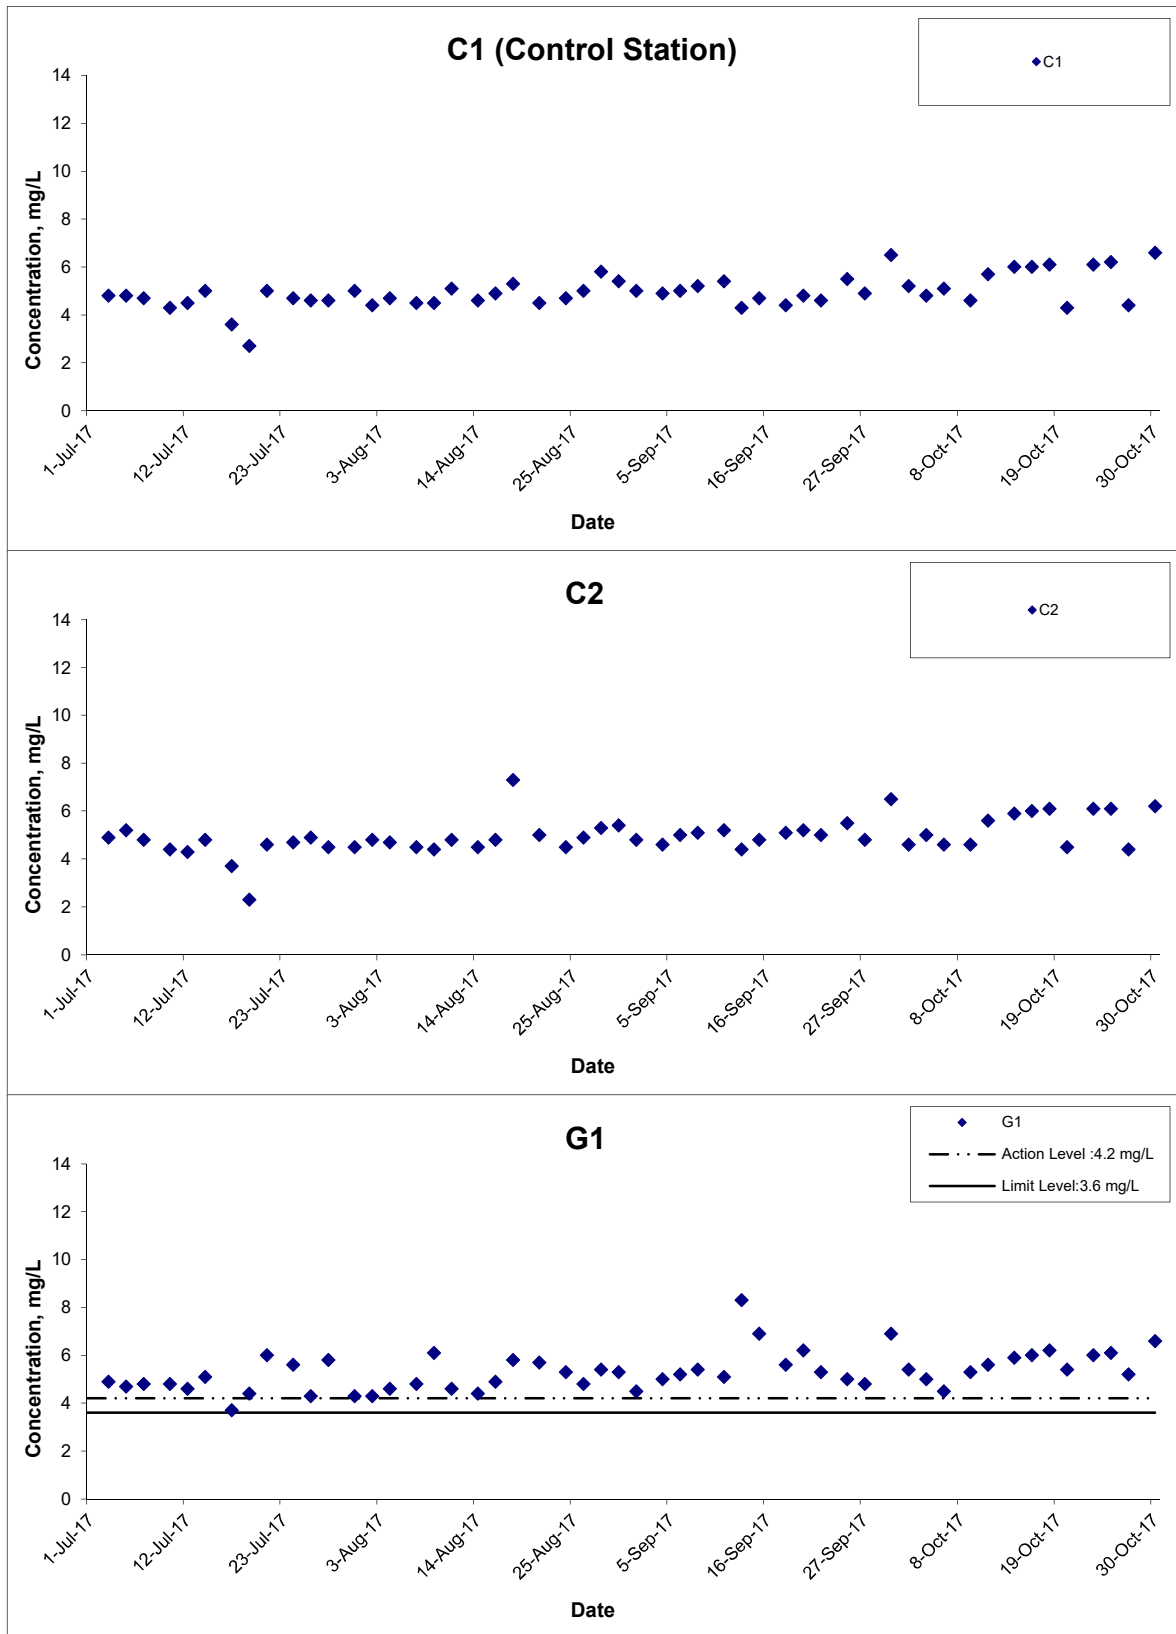

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Dissolved Oxygen (Bottom) at Mid-Flood Tide

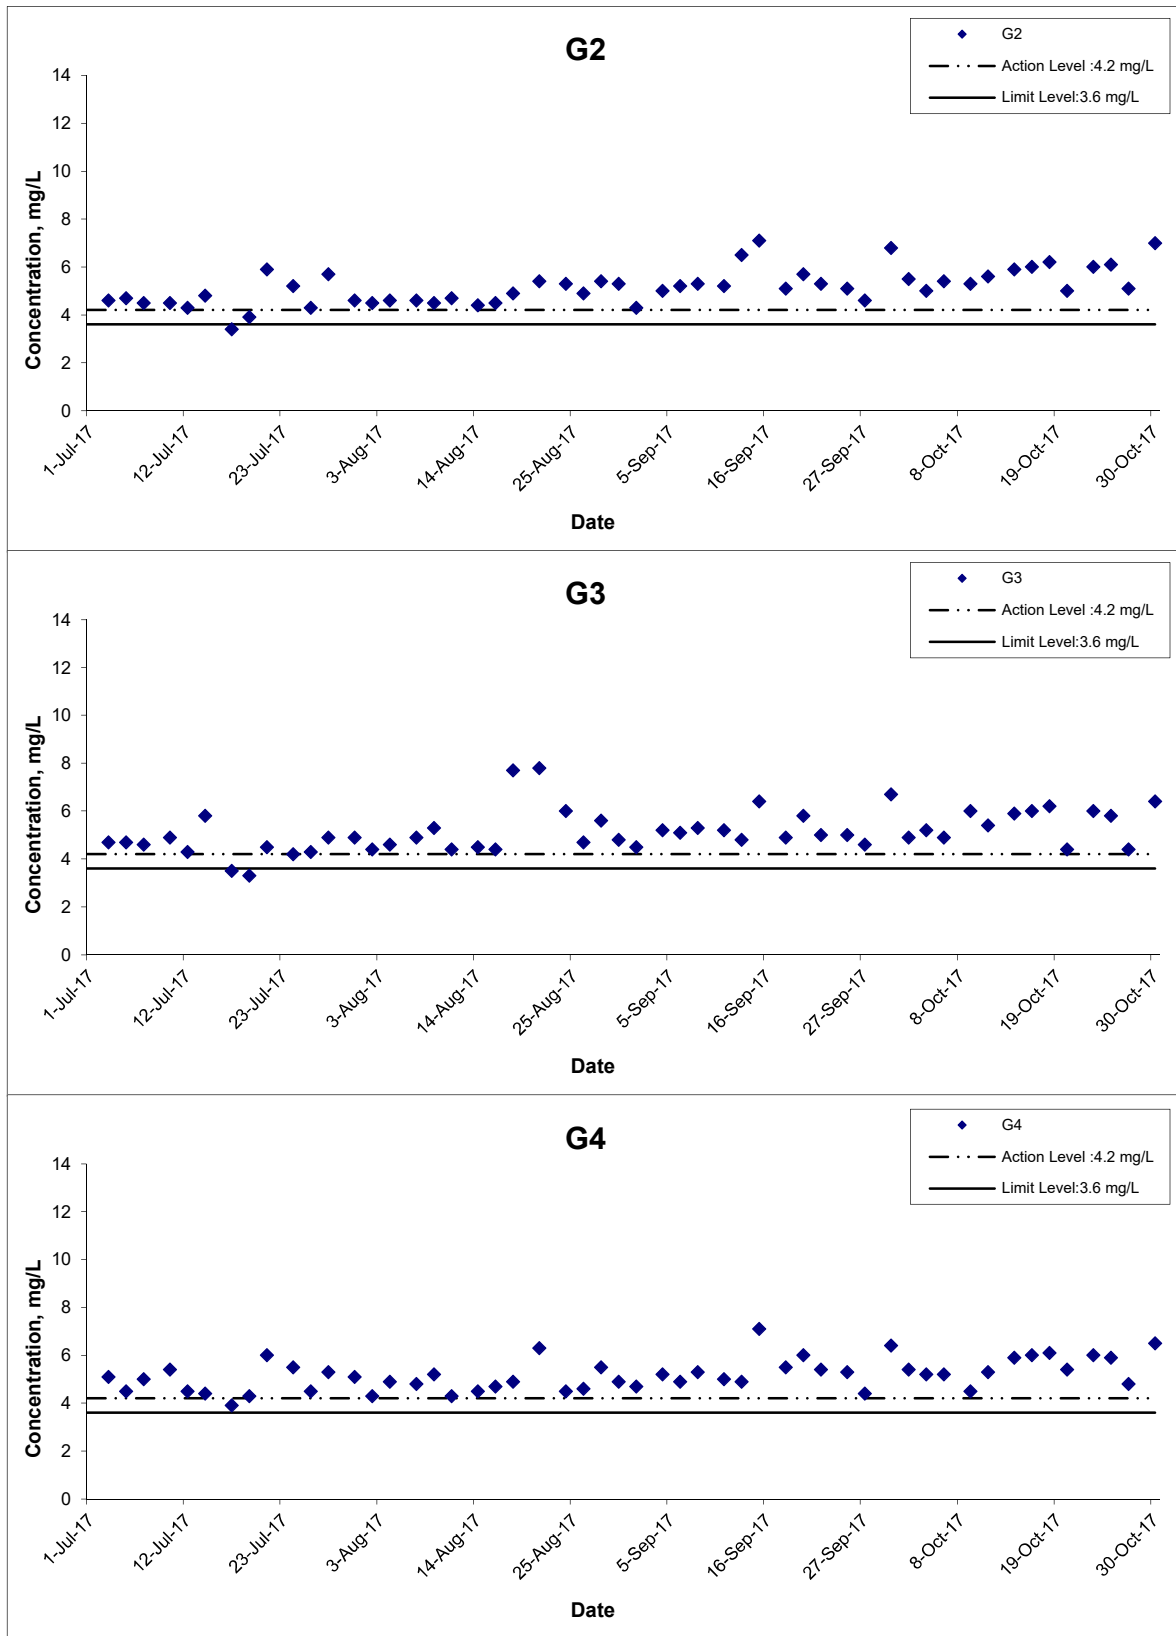




Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I



Dissolved Oxygen (Bottom) at Mid-Flood Tide

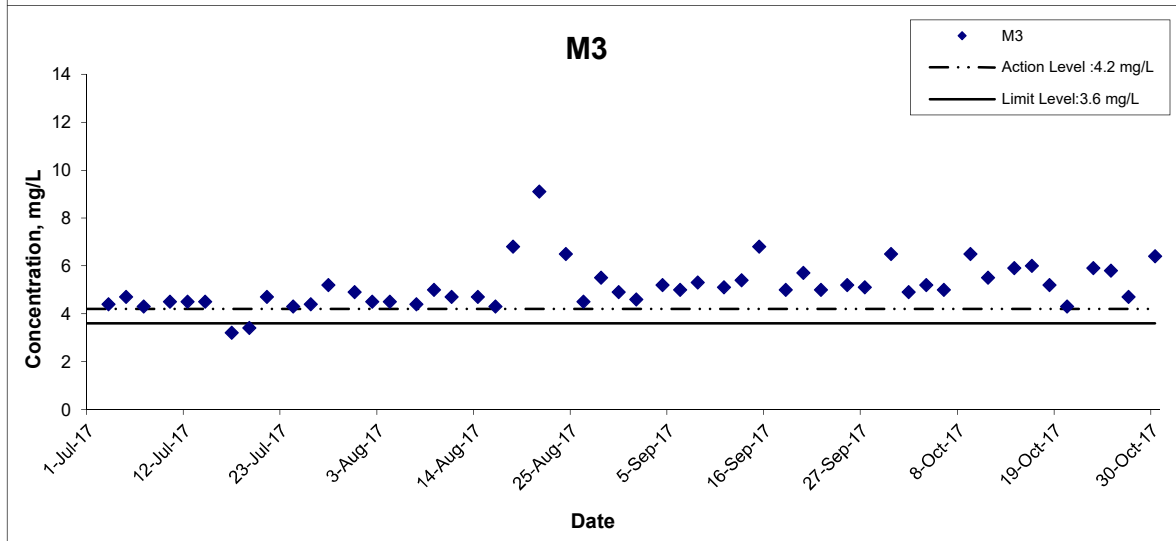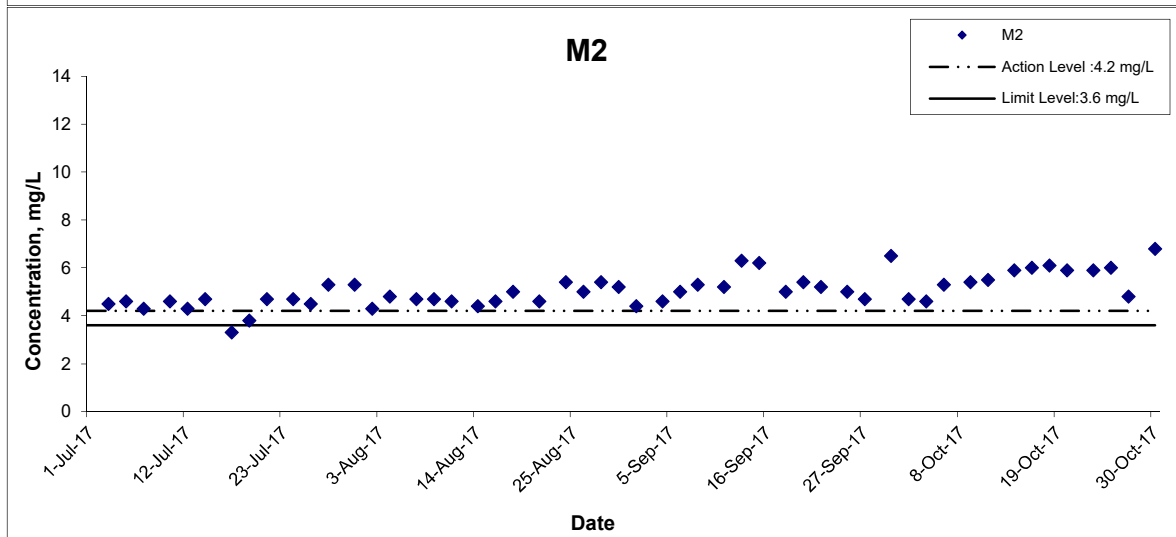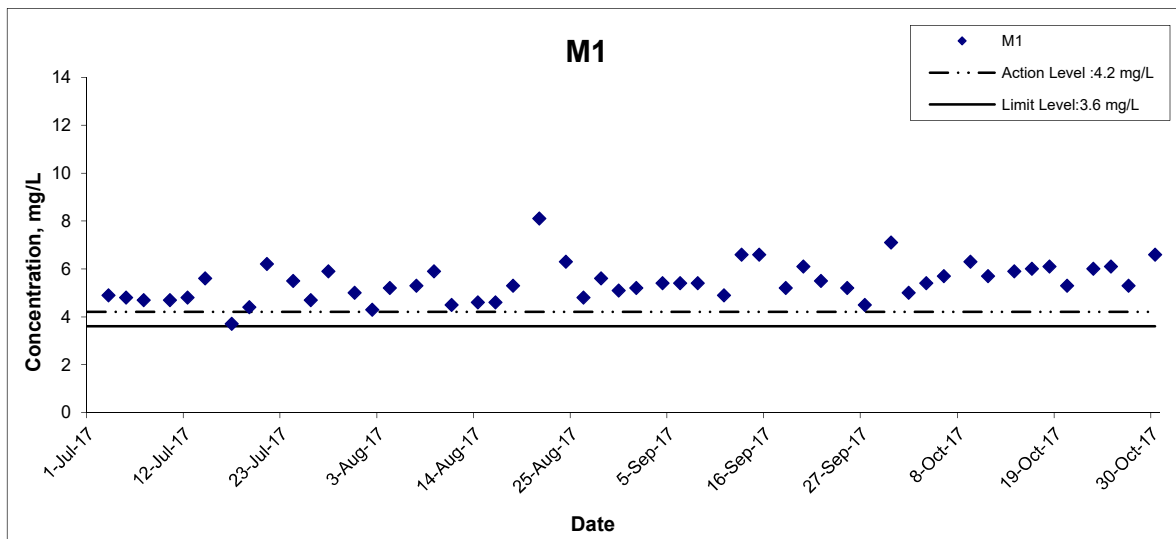

Title

Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring
 Results

Scale

N.T.S

Date

Oct 17

Project No.


MA16034

Appendix

I




Dissolved Oxygen (Bottom) at Mid-Flood Tide

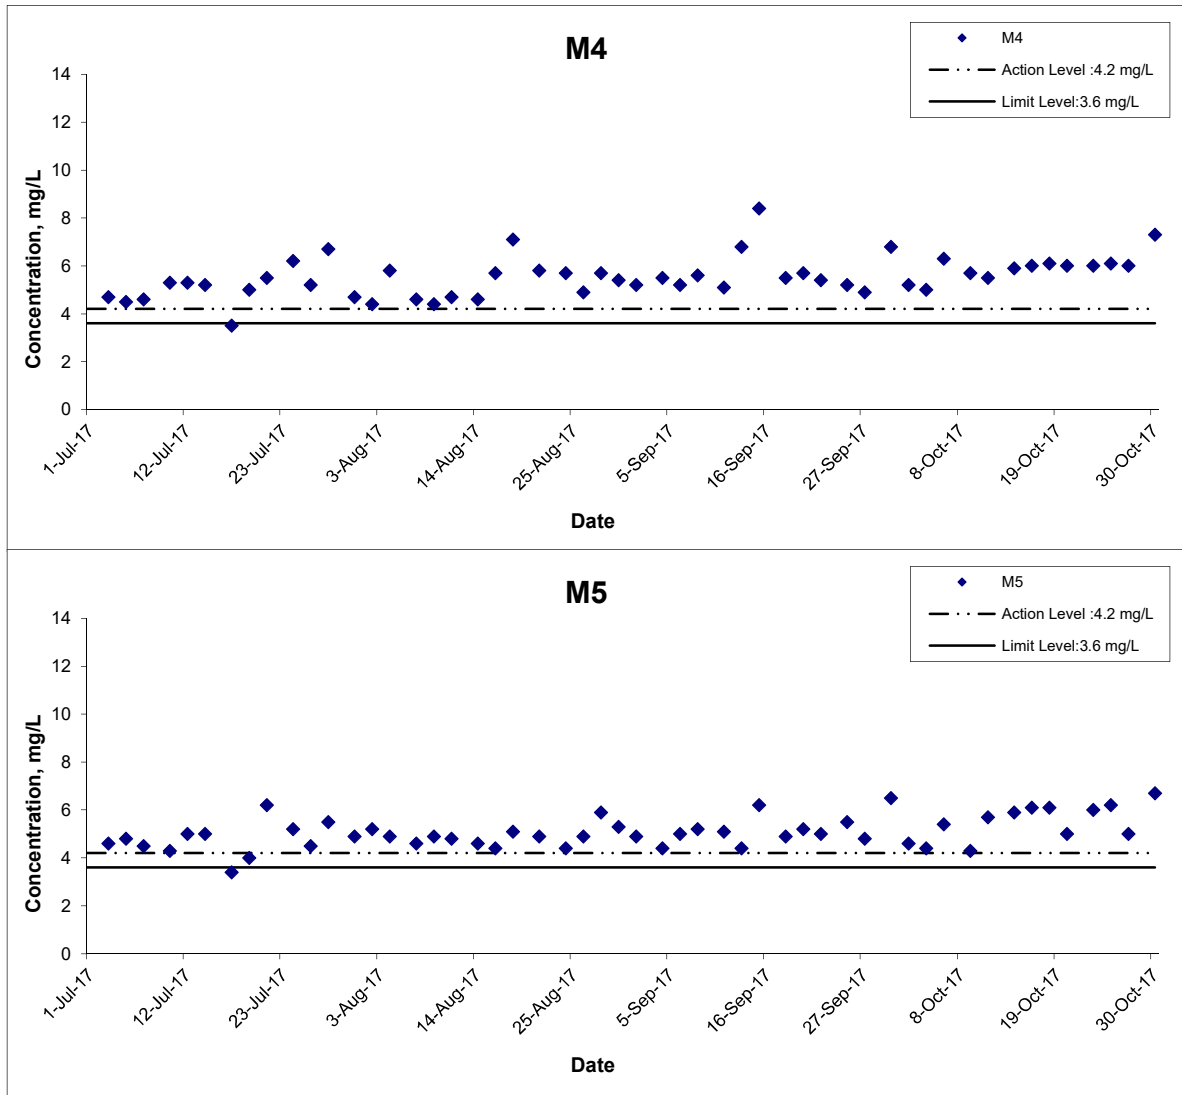


| | | | | | | |
|-------|--|-------|--------|-------------|---------|-----------------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Water Quality Monitoring Results | Date | Oct 17 | Appendix | I | |

Dissolved Oxygen (Intake Level of WSD Salt Water Intake) at Mid-Ebb Tide

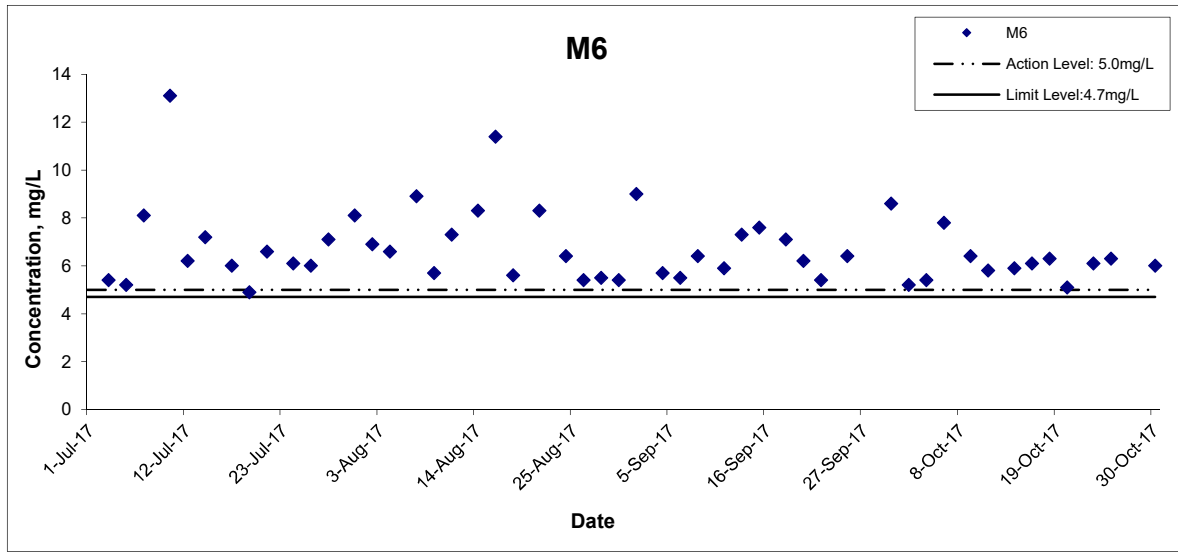


| | | | | | | |
|-------|--|-------|--------|-------------|---------|-----------------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Water Quality Monitoring Results | Date | Oct 17 | Appendix | I | |

Dissolved Oxygen (Intake Level of WSD Salt Water Intake) at Mid-Flood Tide

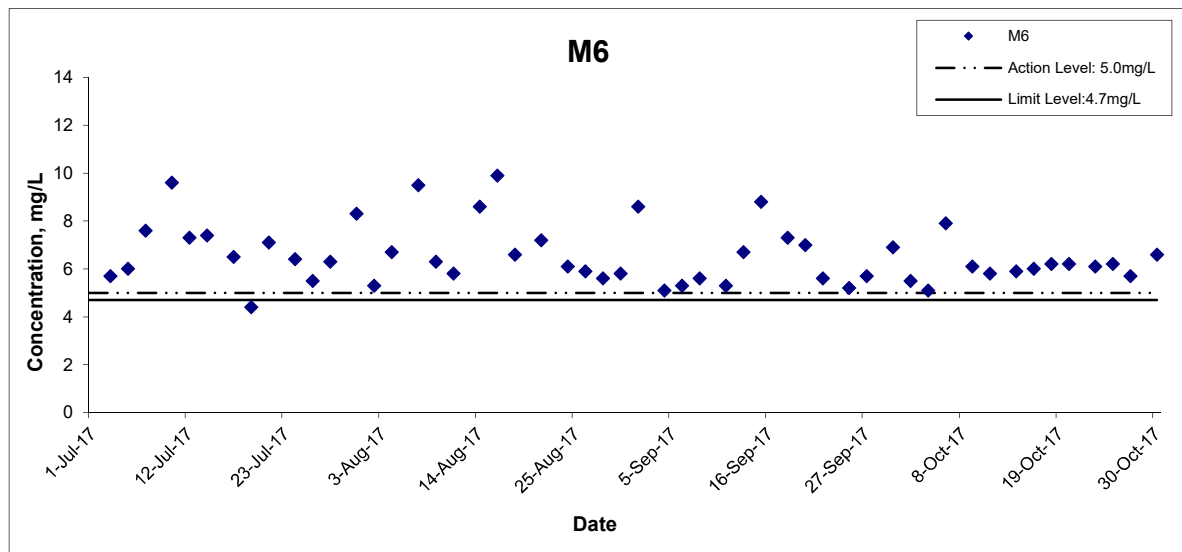

| | | | | | |
|---|-------|--------|-------------|---------|----------|
| Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Water Quality Monitoring Results | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Date | Oct 17 | Appendix | I | |

Turbidity (Depth-averaged) at Mid-Ebb Tide

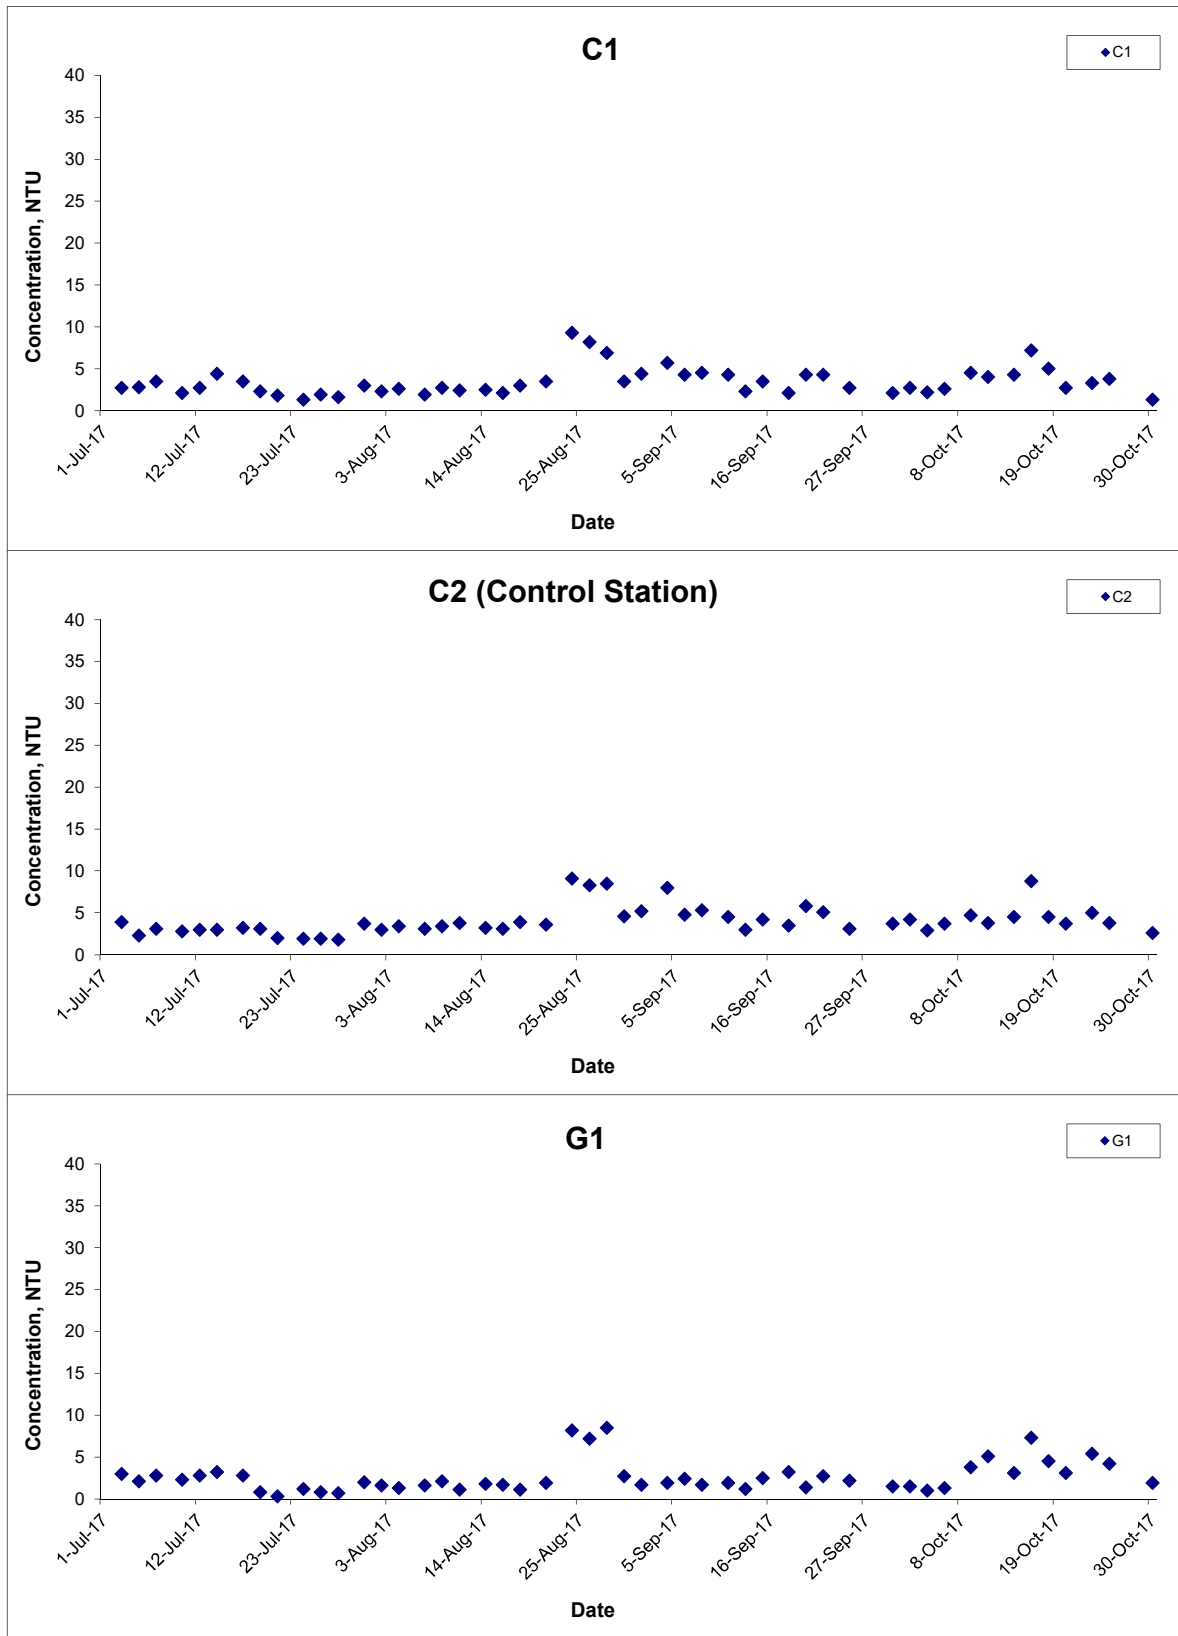


Title
 Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I



Turbidity (Depth-averaged) at Mid-Ebb Tide

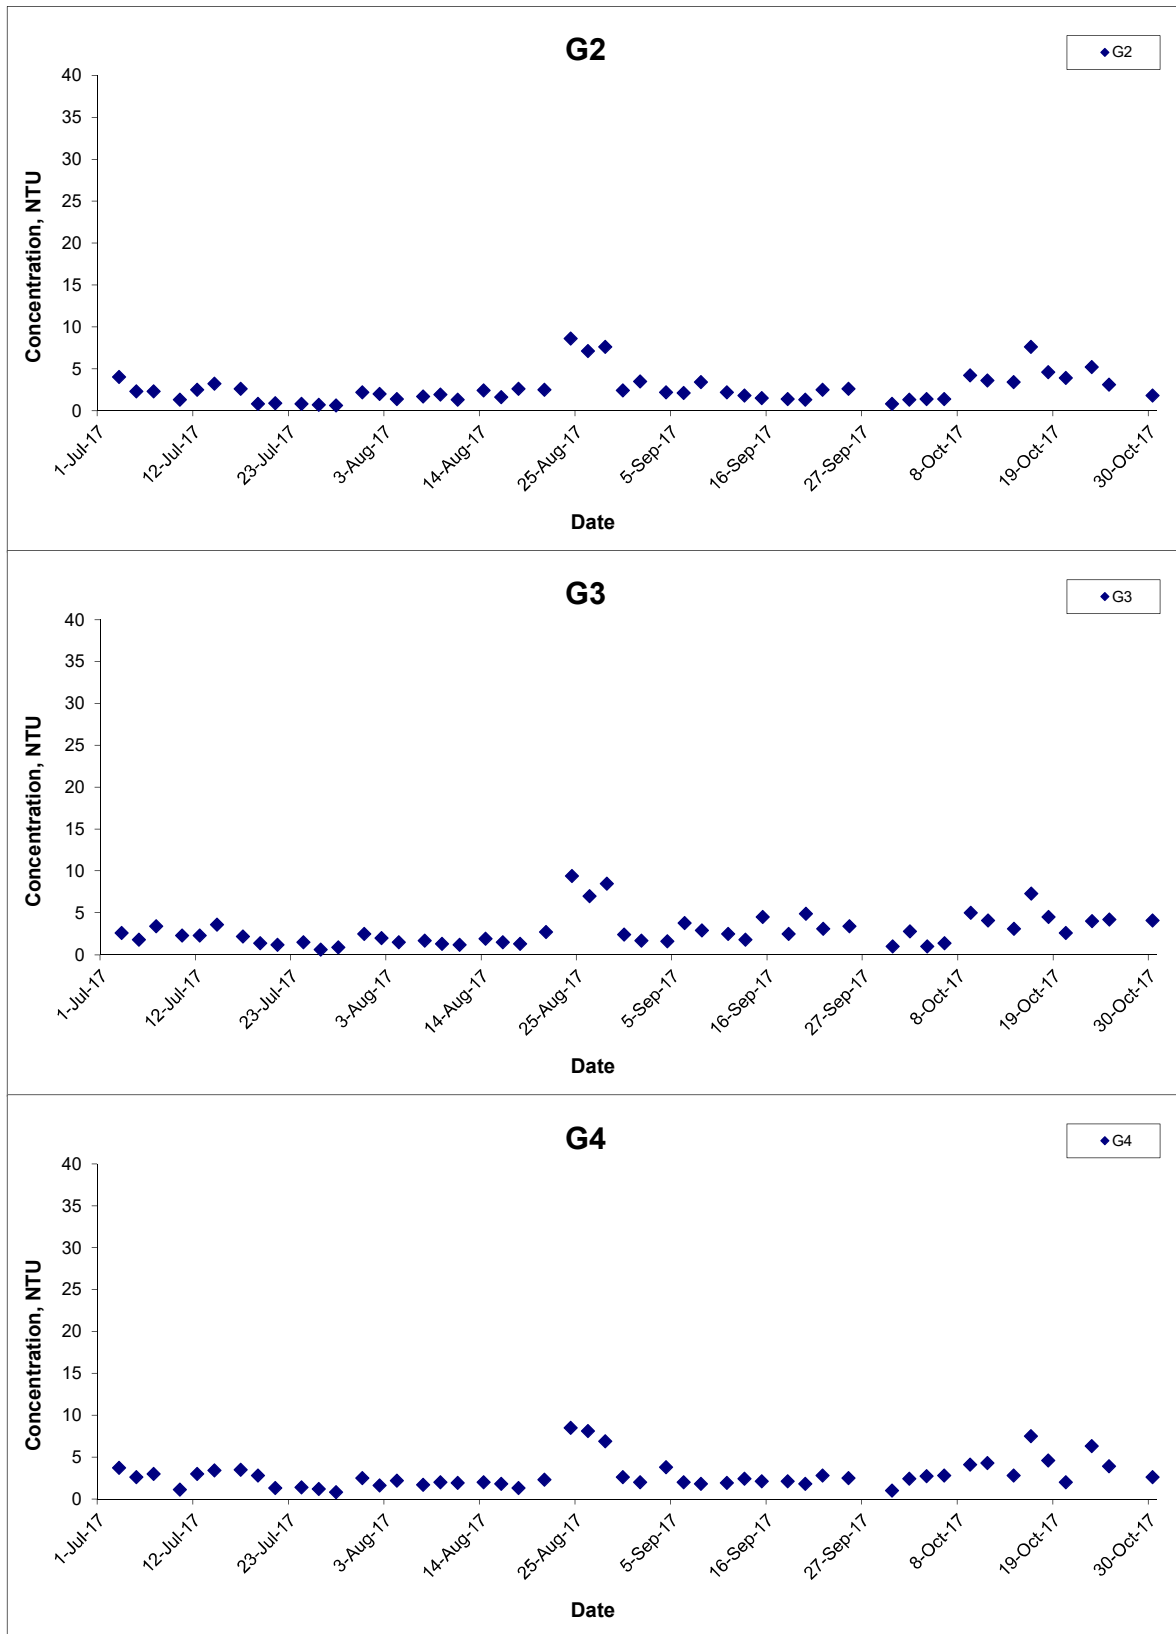

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Turbidity (Depth-averaged) at Mid-Ebb Tide

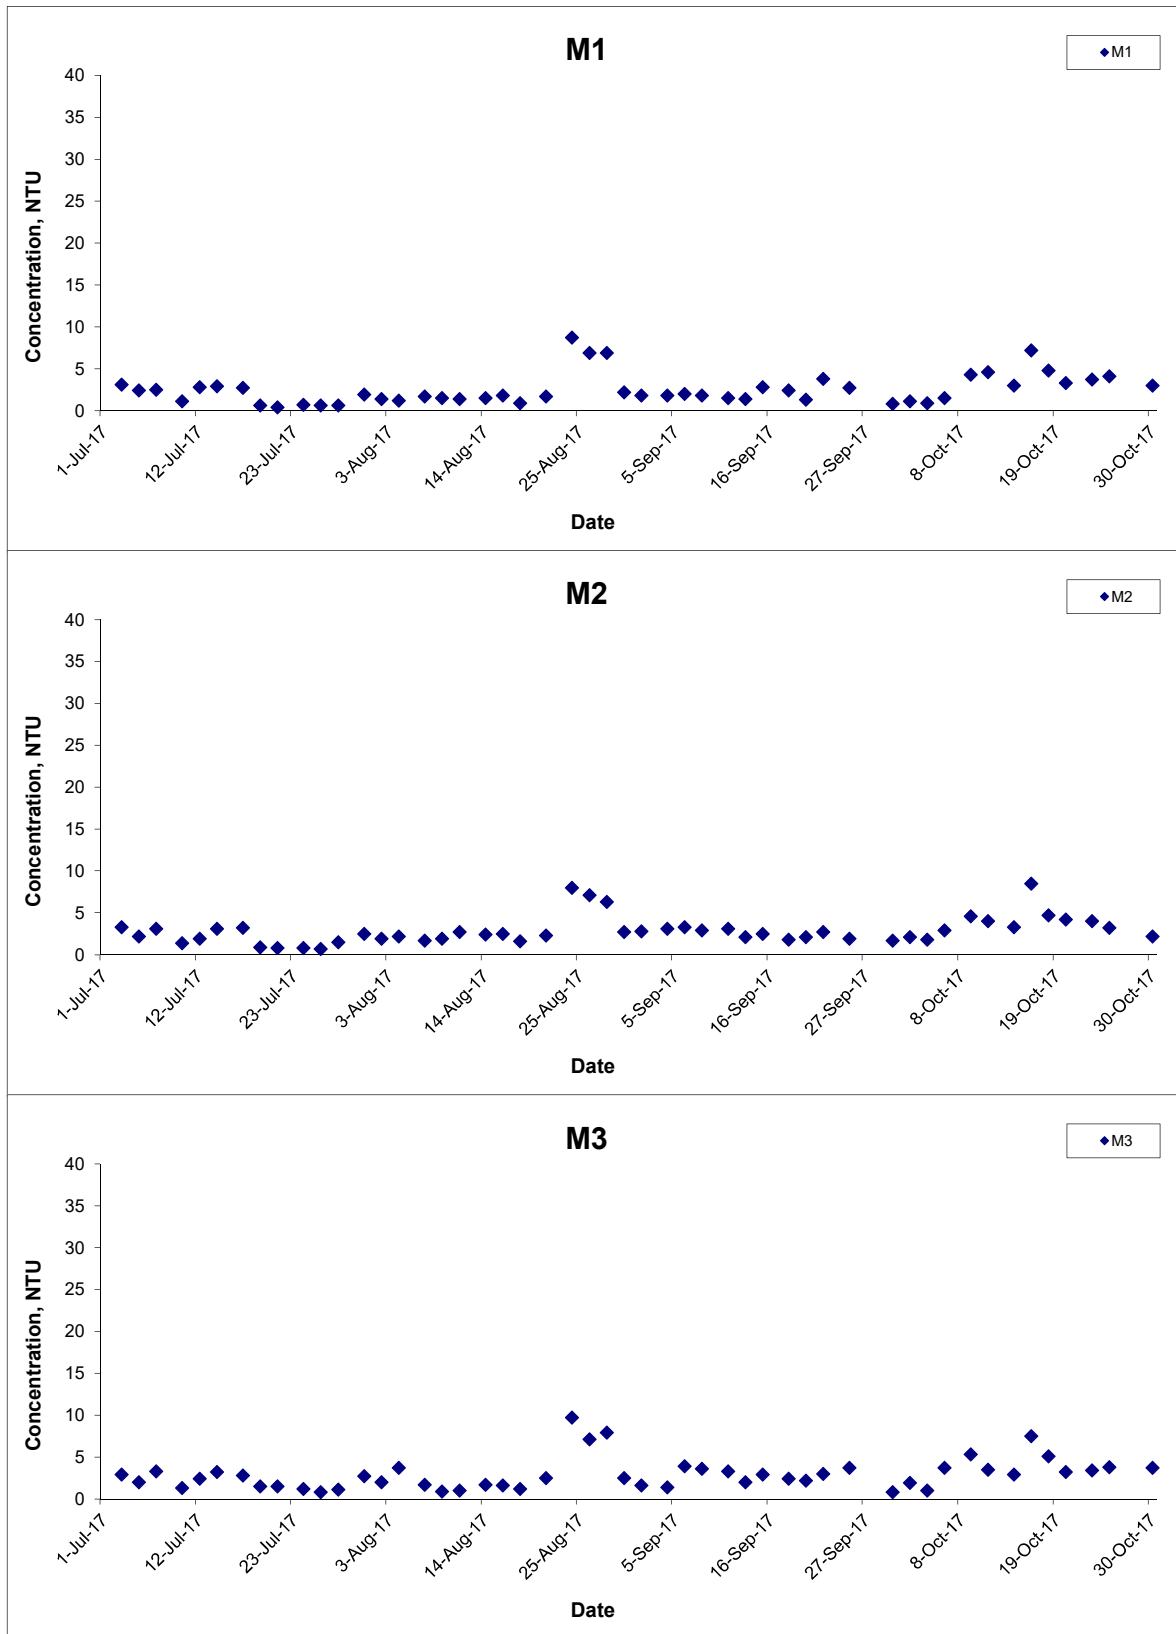


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I




Turbidity (Depth-averaged) at Mid-Ebb Tide

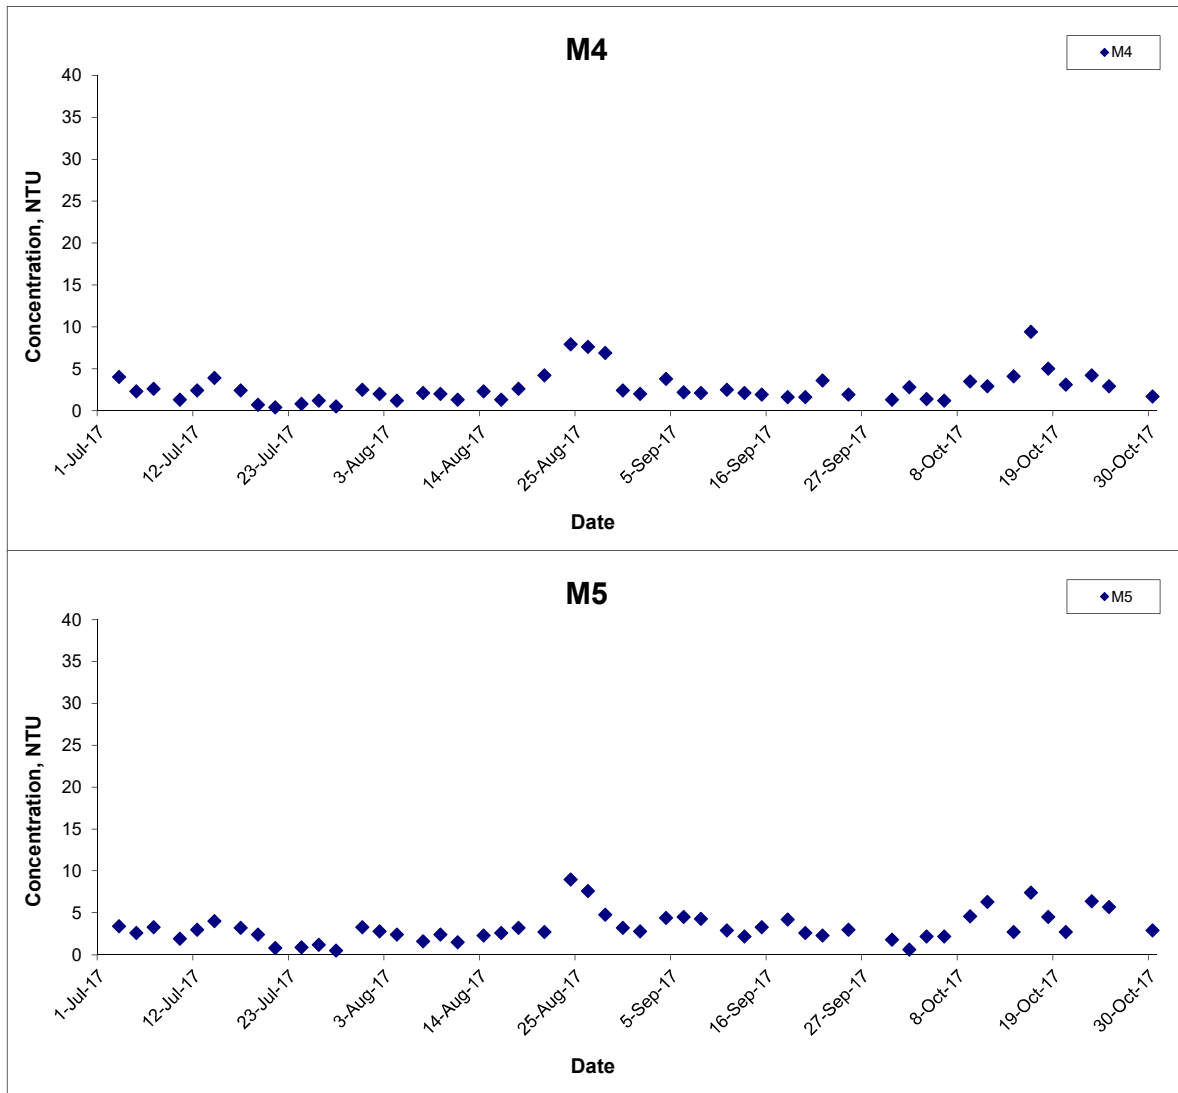

| | | | |
|---|----------------|------------------------|----------|
| Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Water Quality Monitoring Results | Scale N.T.S | Project No. MA16034 | CINOTECH |
| | Date Oct 17 | Appendix I | |

Turbidity (Depth-averaged) at Mid-Flood Tide

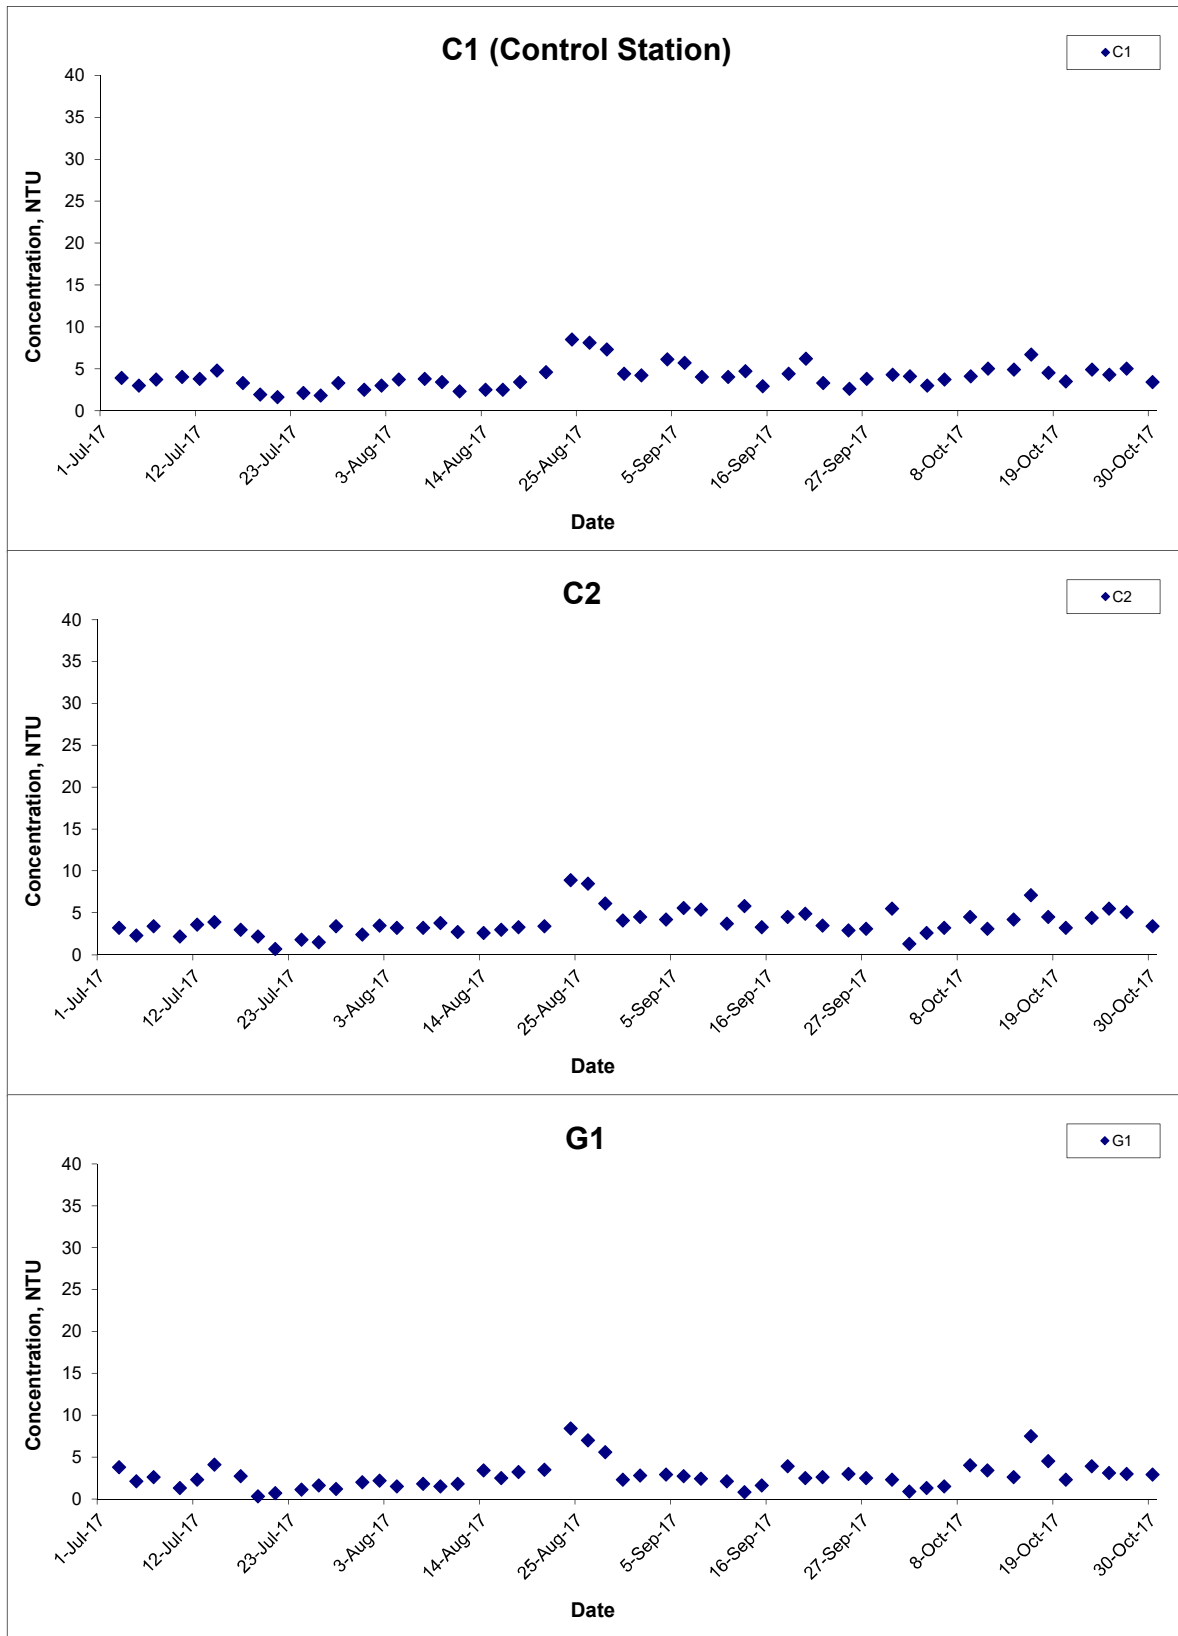


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I



Turbidity (Depth-averaged) at Mid-Flood Tide

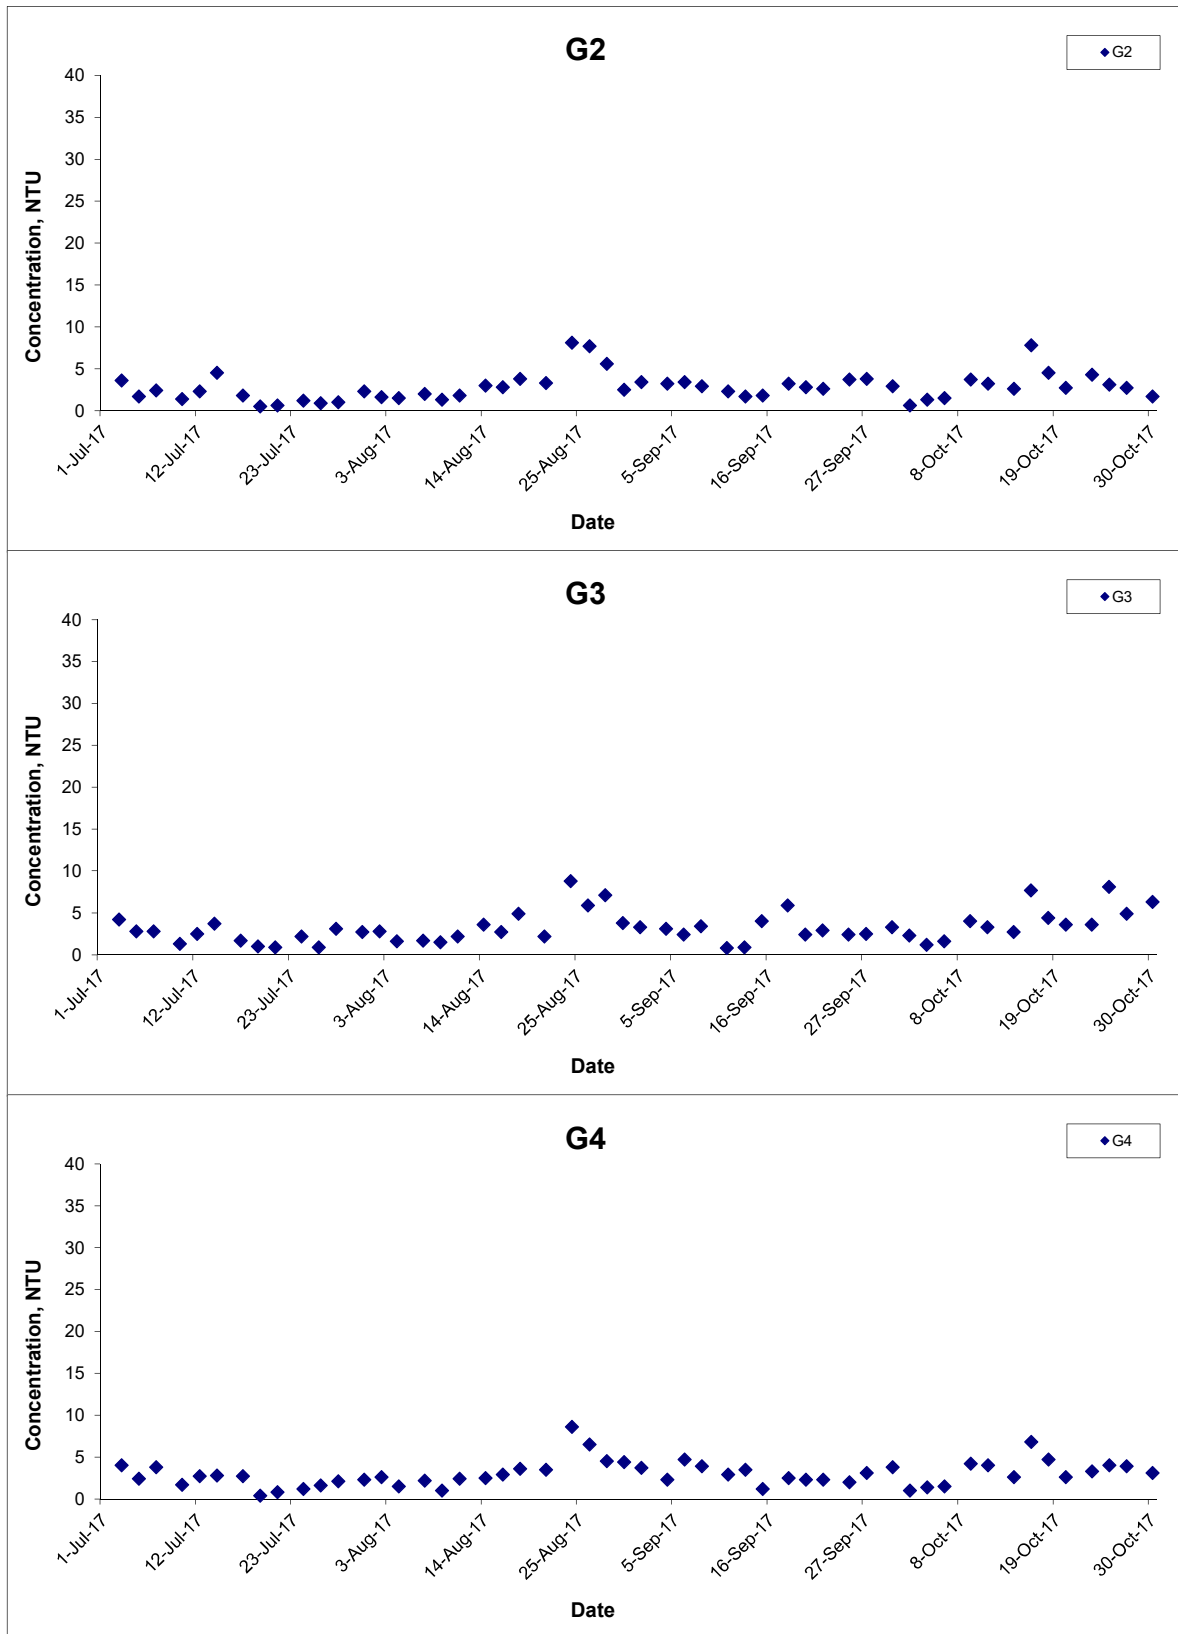

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Turbidity (Depth-averaged) at Mid-Flood Tide

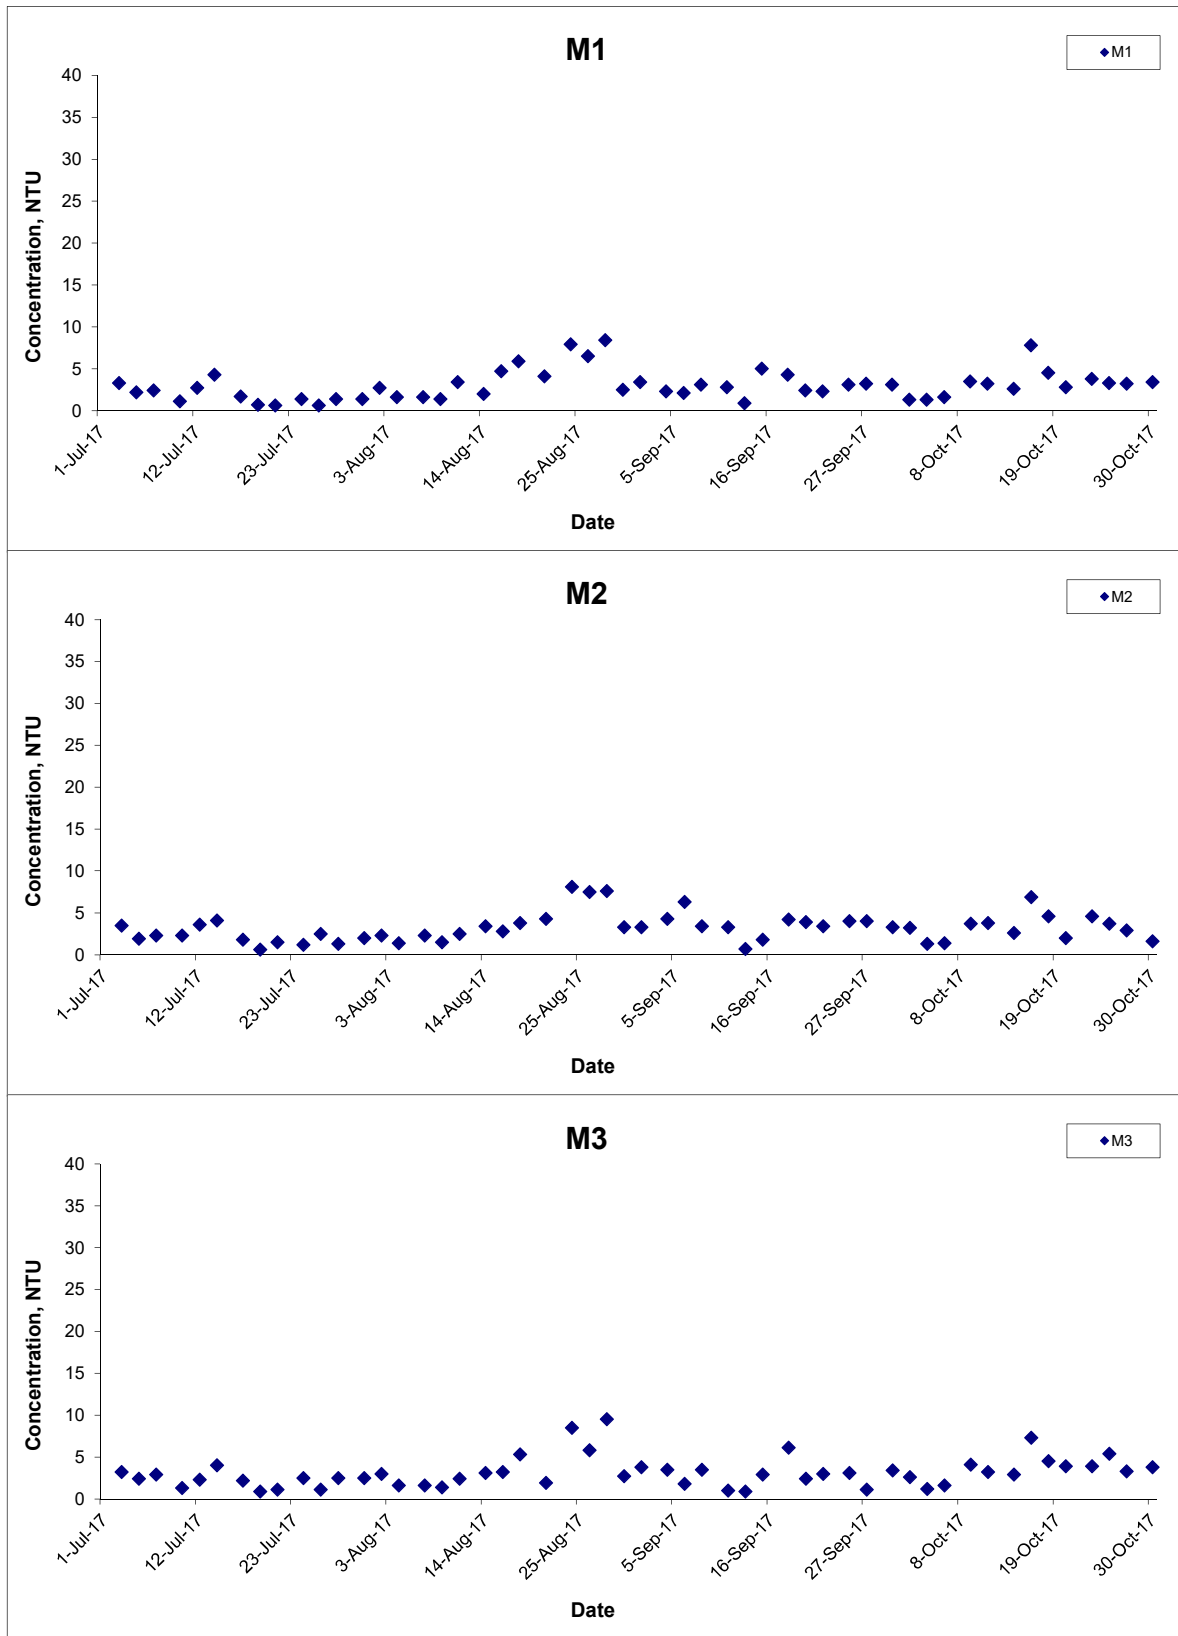


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I




Turbidity (Depth-averaged) at Mid-Flood Tide

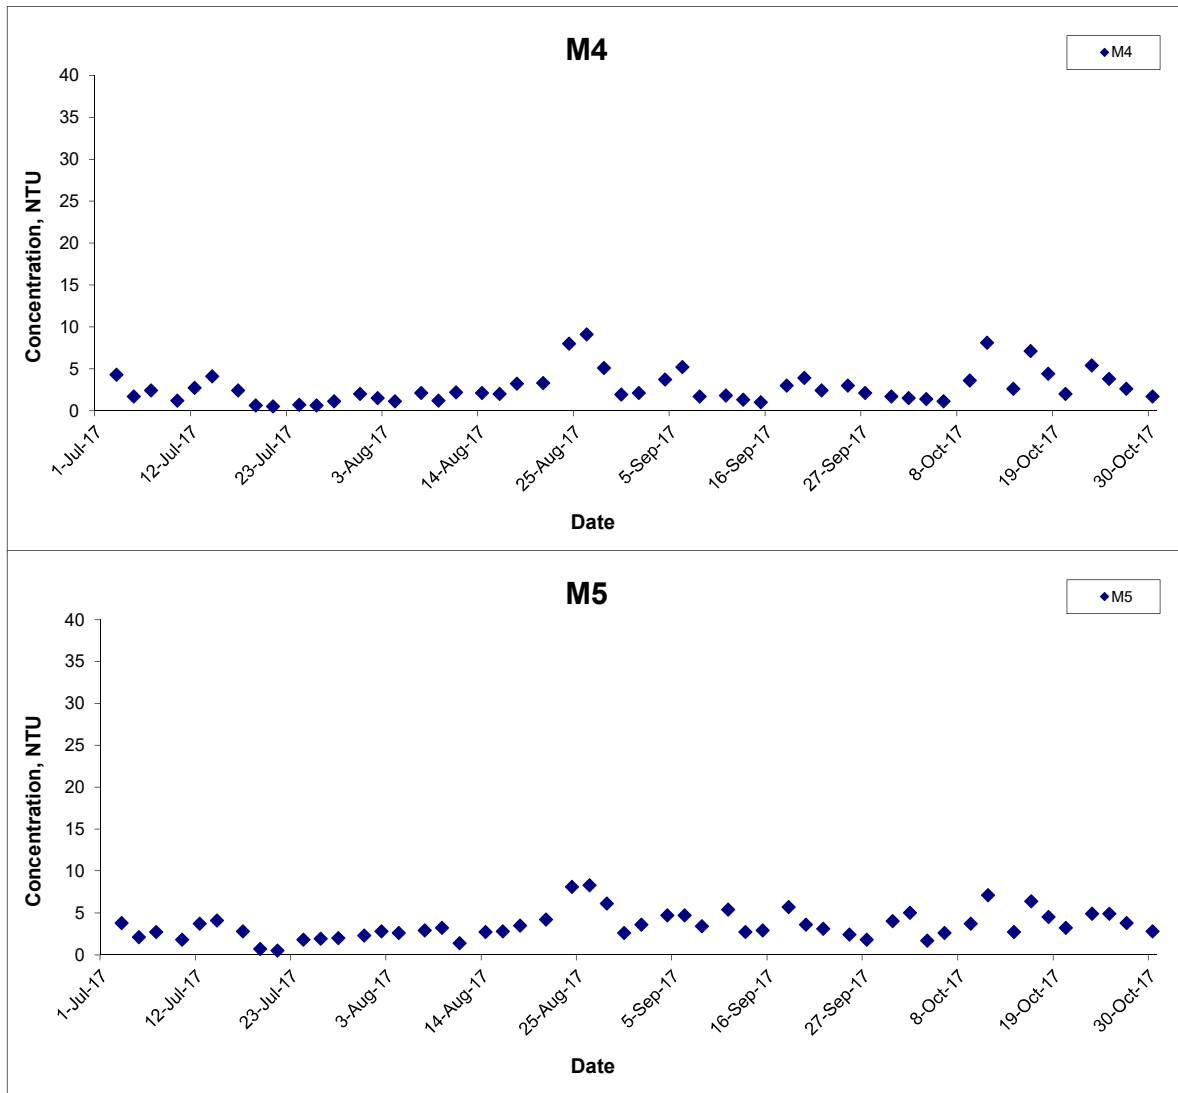

| | | | | | | |
|-------|--|-------|--------|-------------|---------|-----------------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Water Quality Monitoring Results | Date | Oct 17 | Appendix | I | |

Turbidity (Bottom) at Mid-Ebb Tide

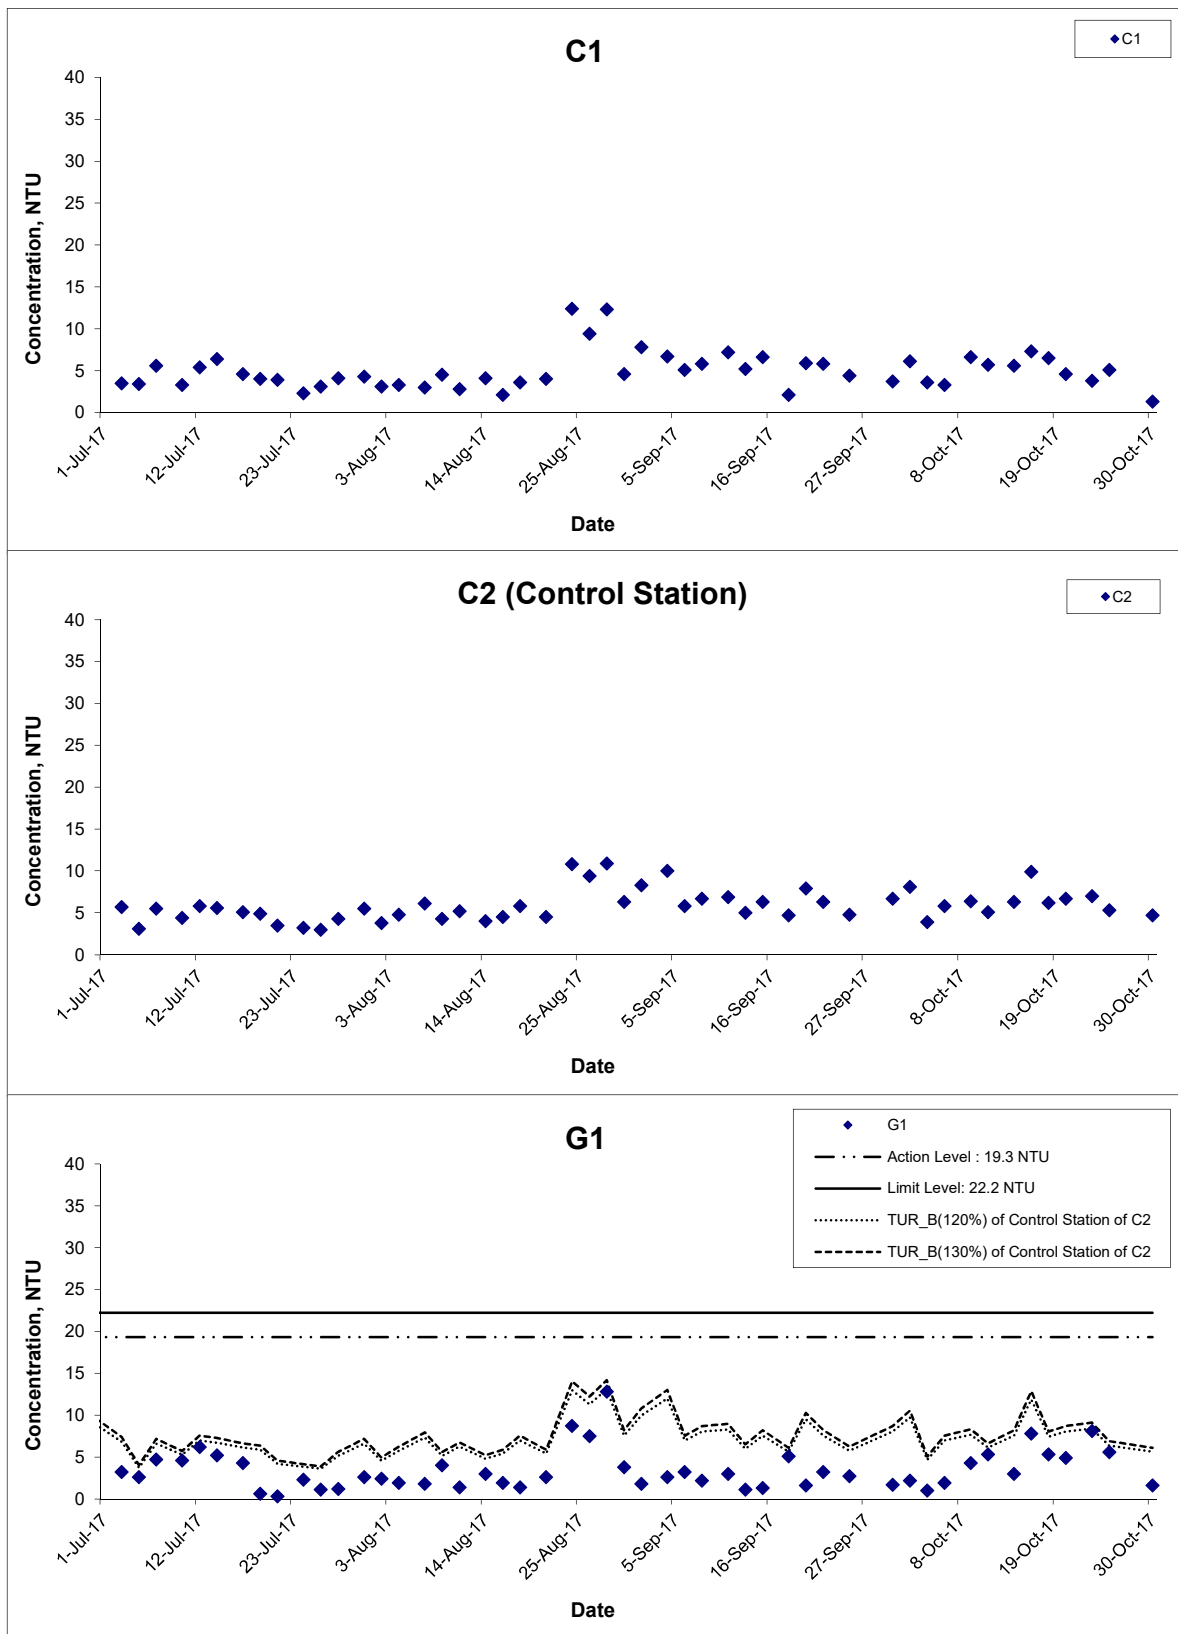

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Ebb Tide

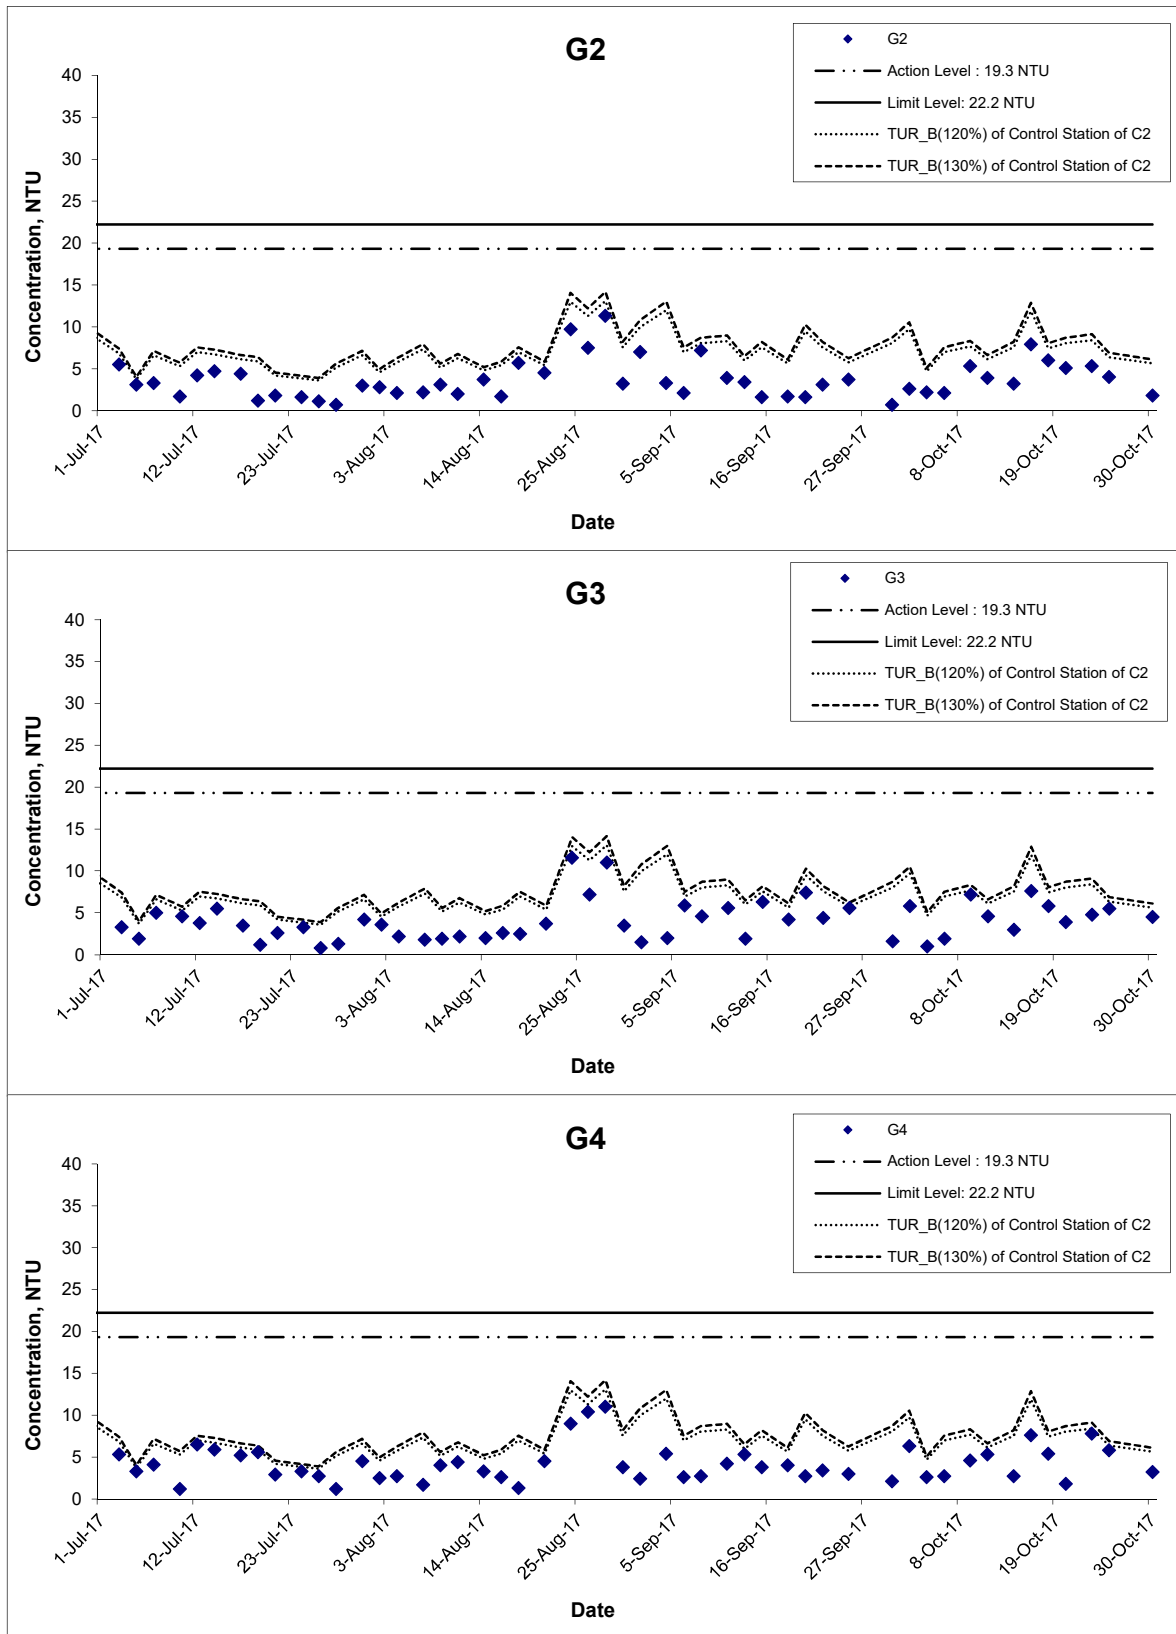


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
 Date
 Oct 17

Project
 No. MA16034
 Appendix
 I



Turbidity (Bottom) at Mid-Ebb Tide

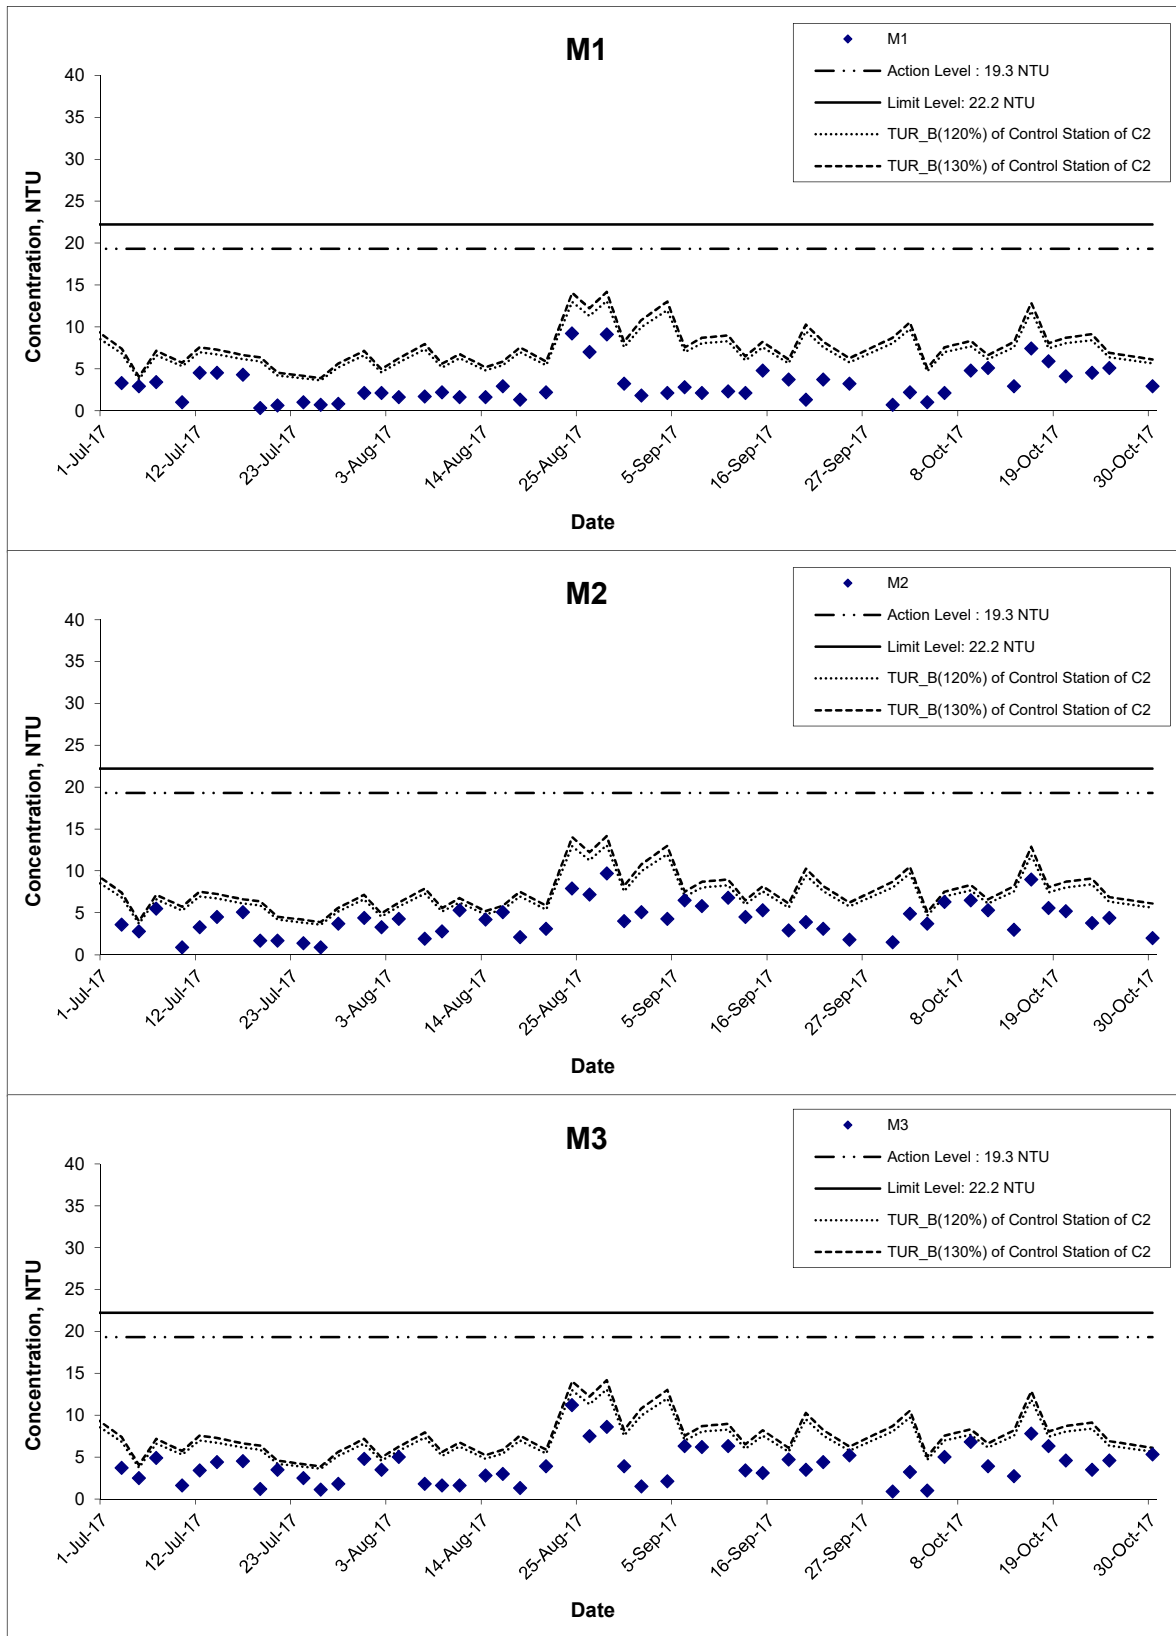

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Ebb Tide

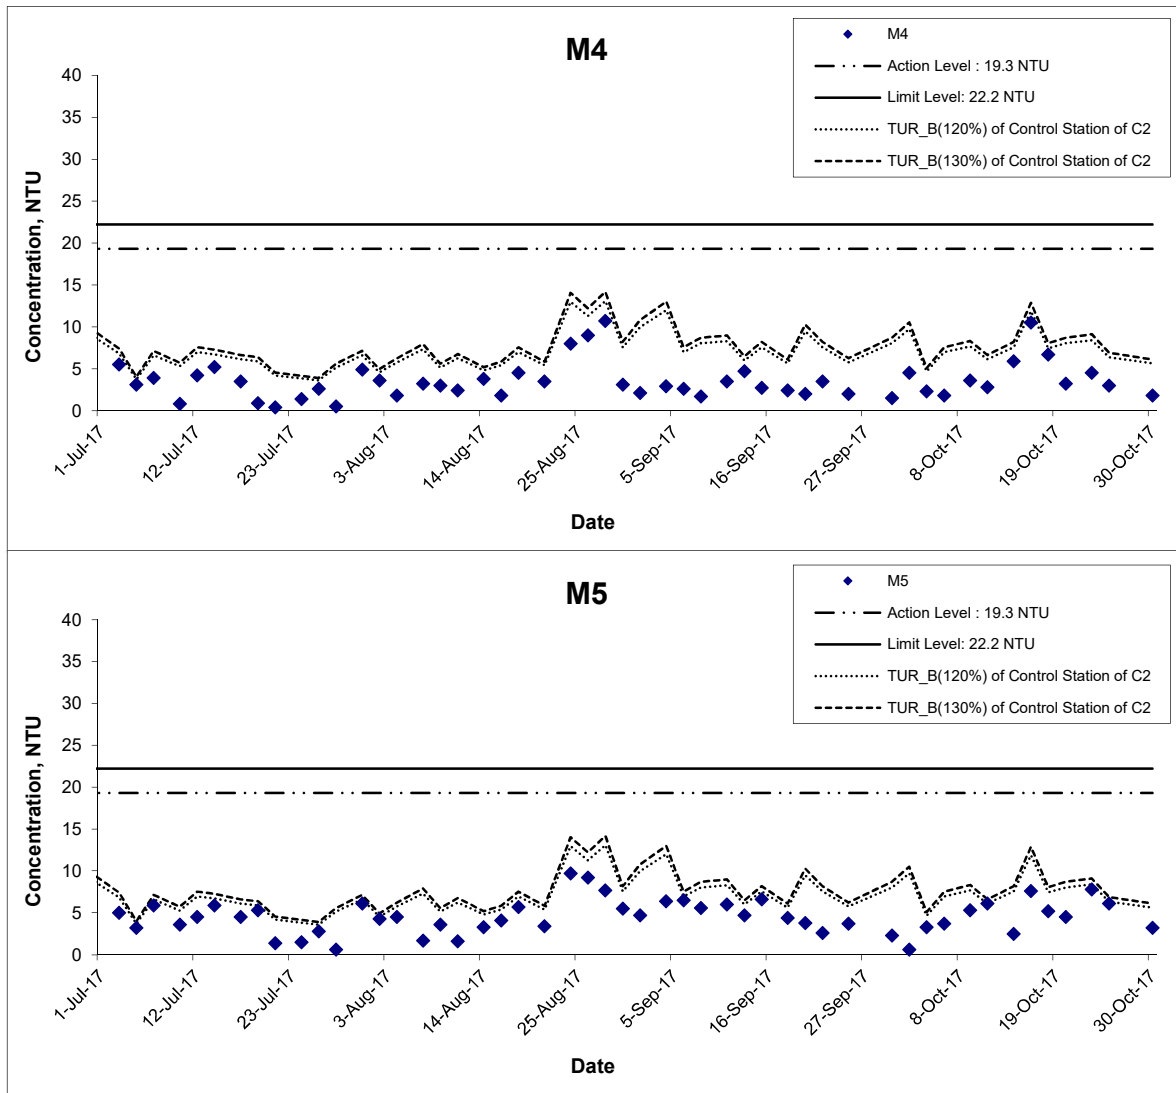

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Flood Tide

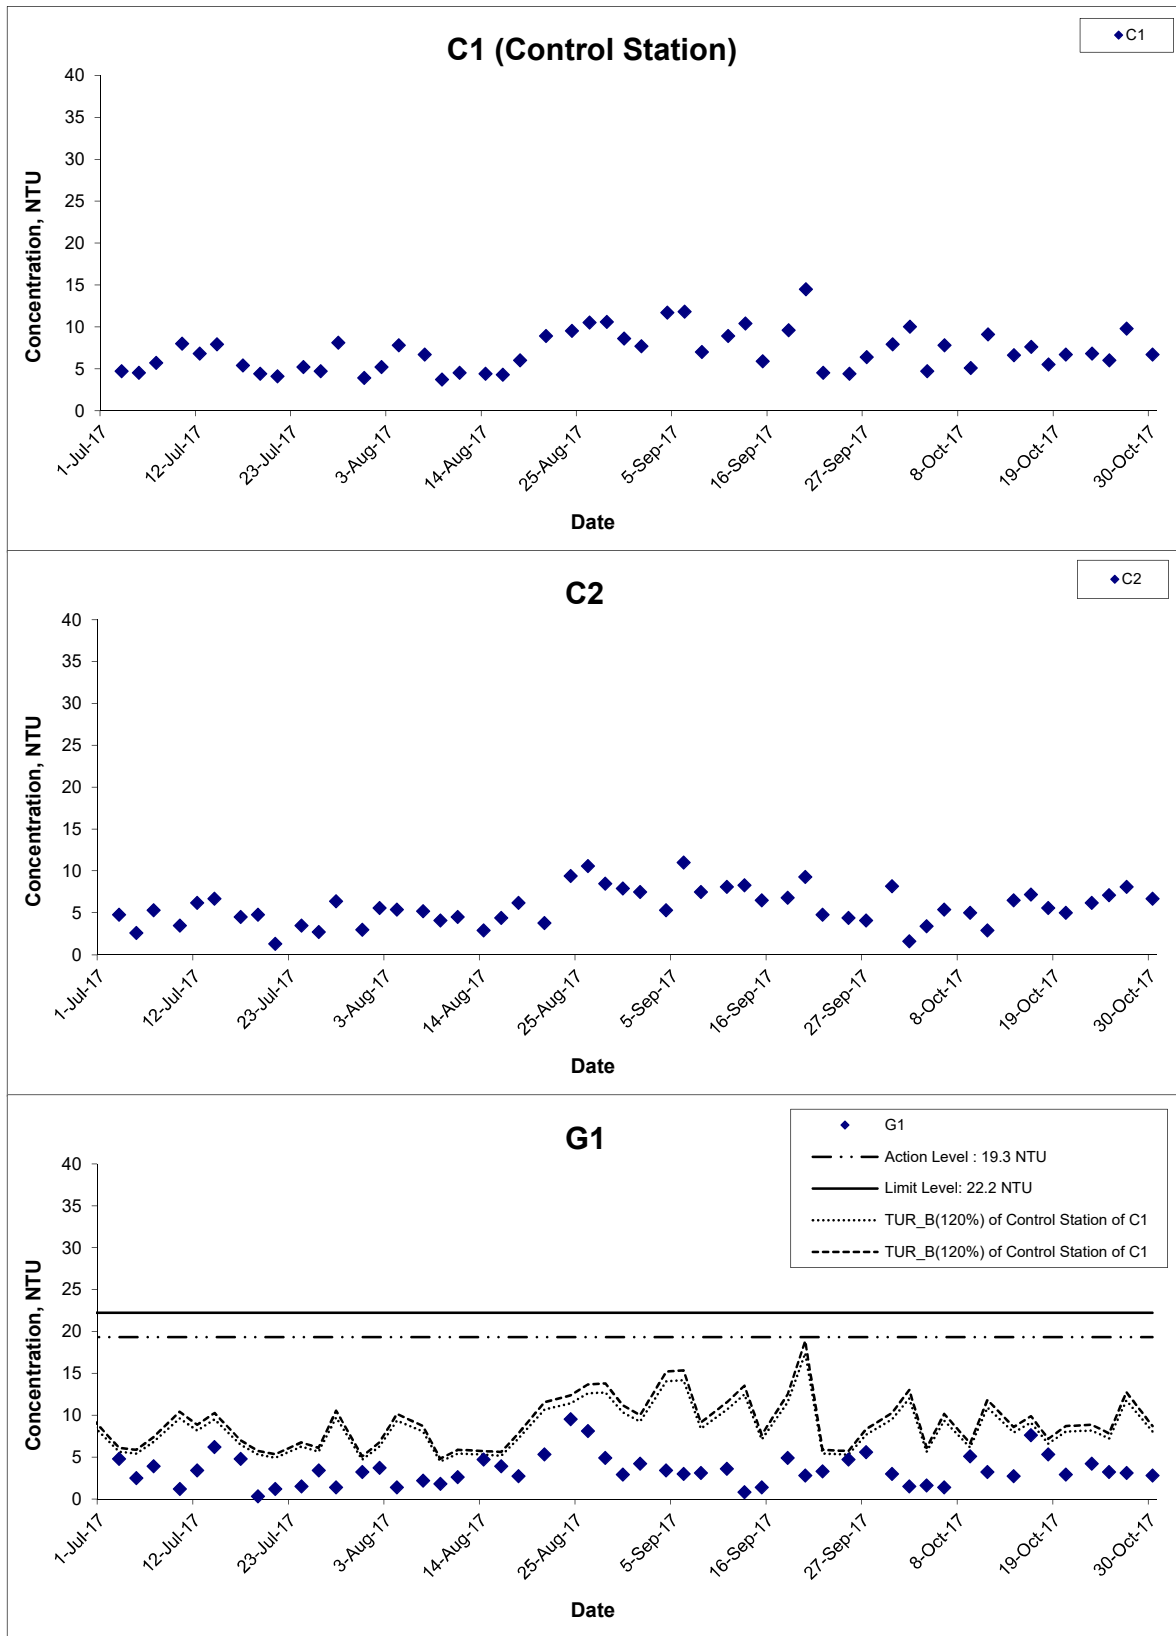

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S




Date Oct 17

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Flood Tide

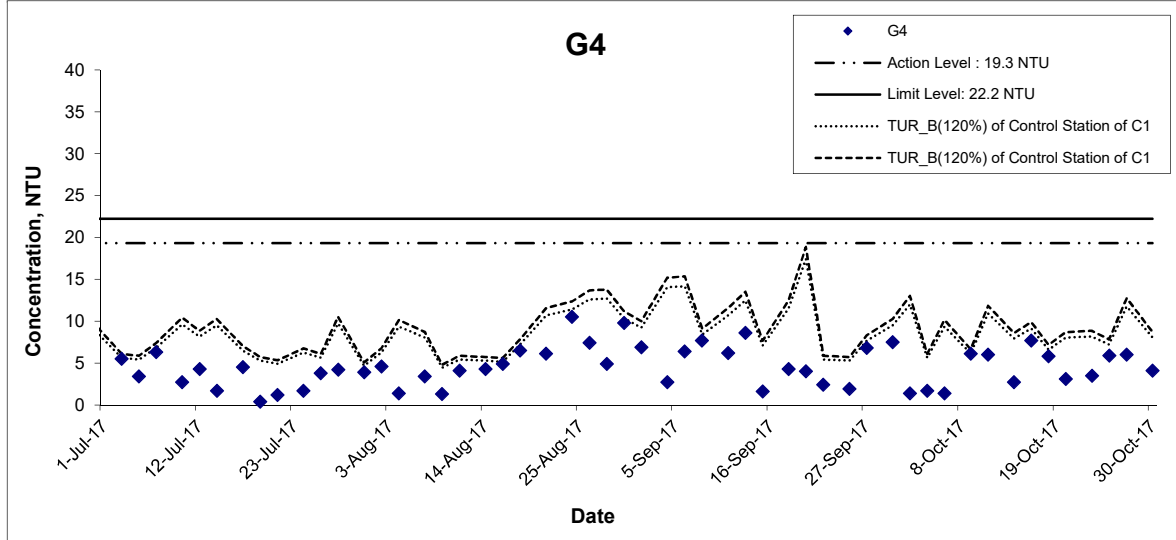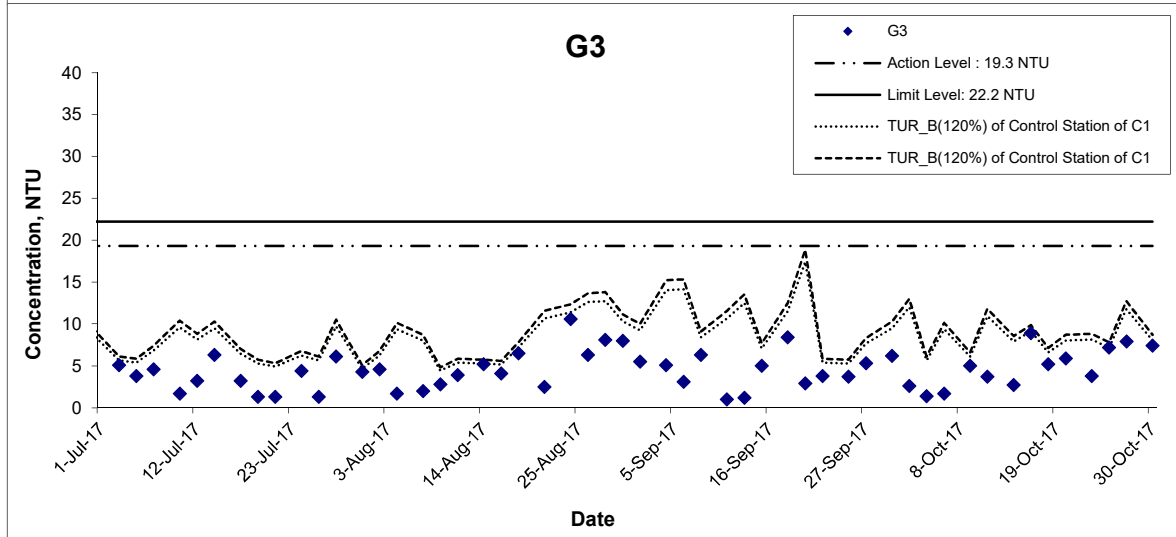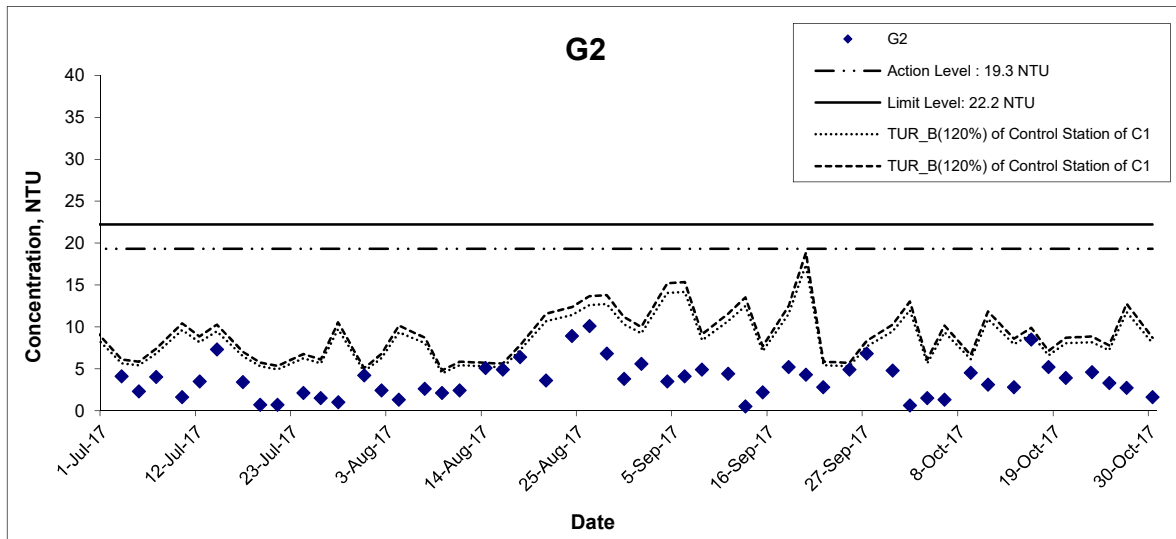

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Flood Tide

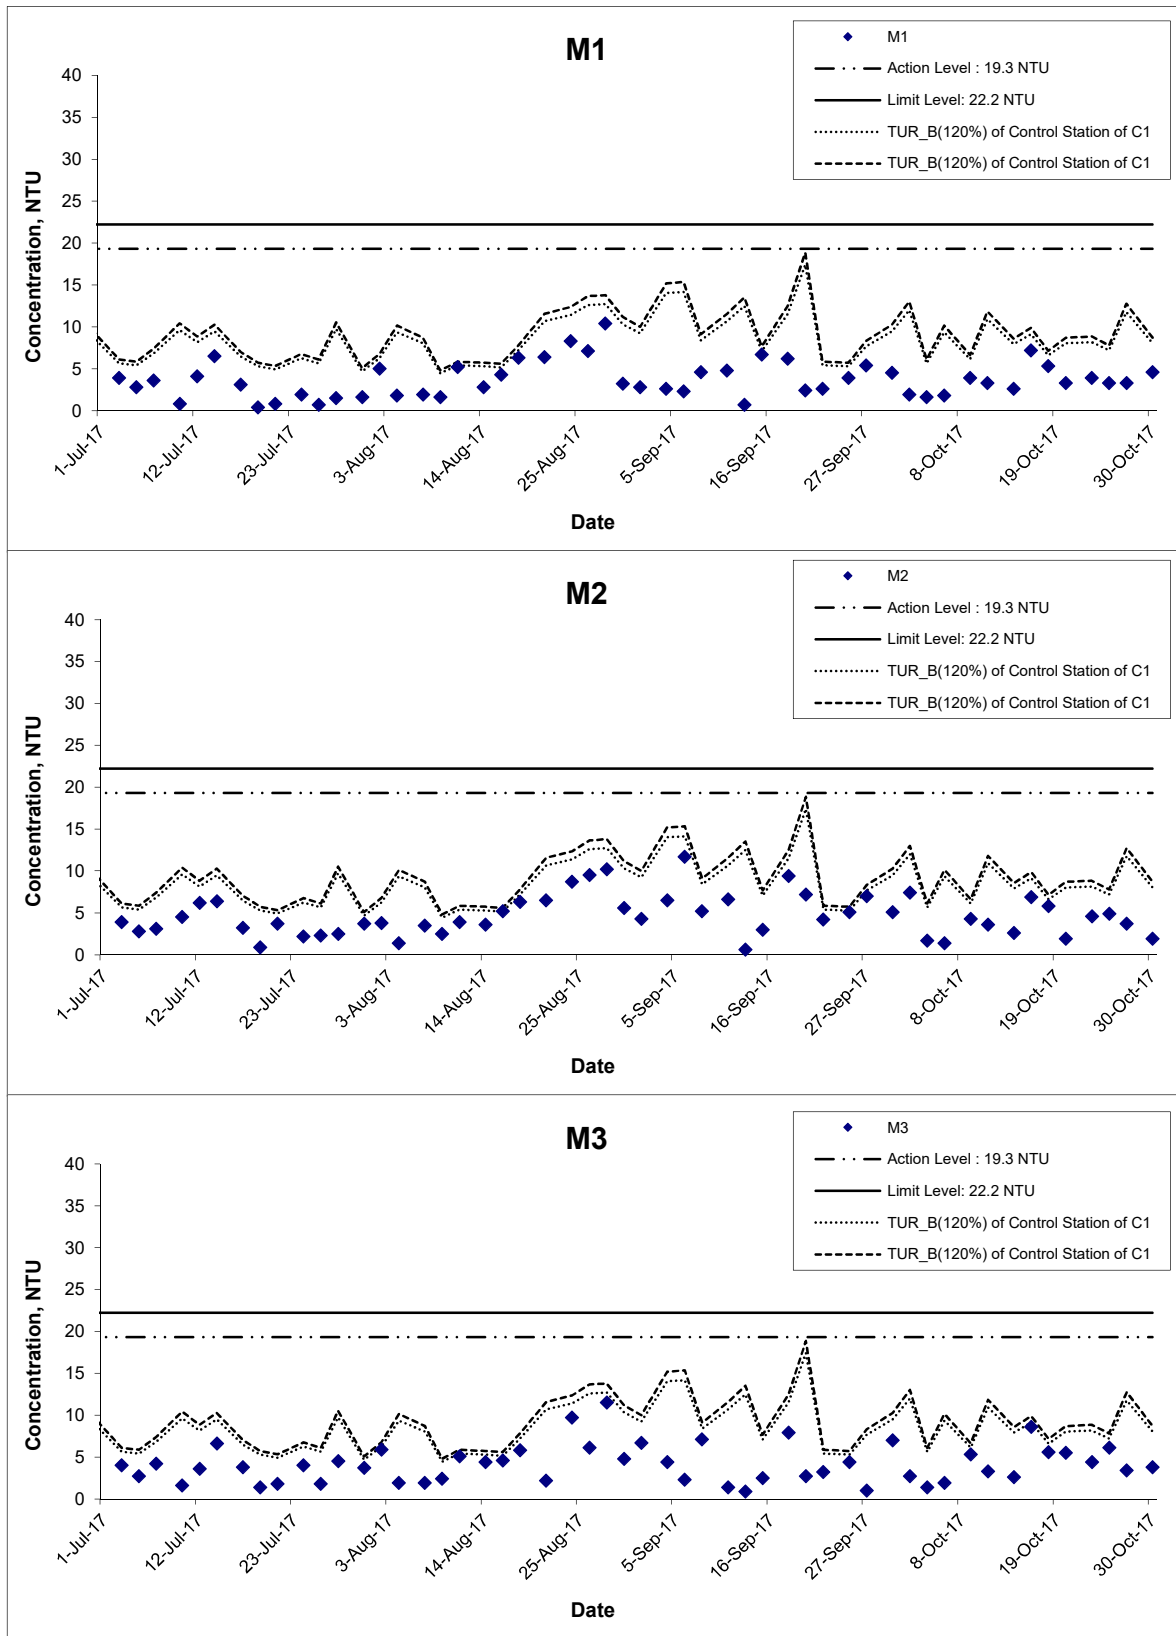

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I




Turbidity (Bottom) at Mid-Flood Tide

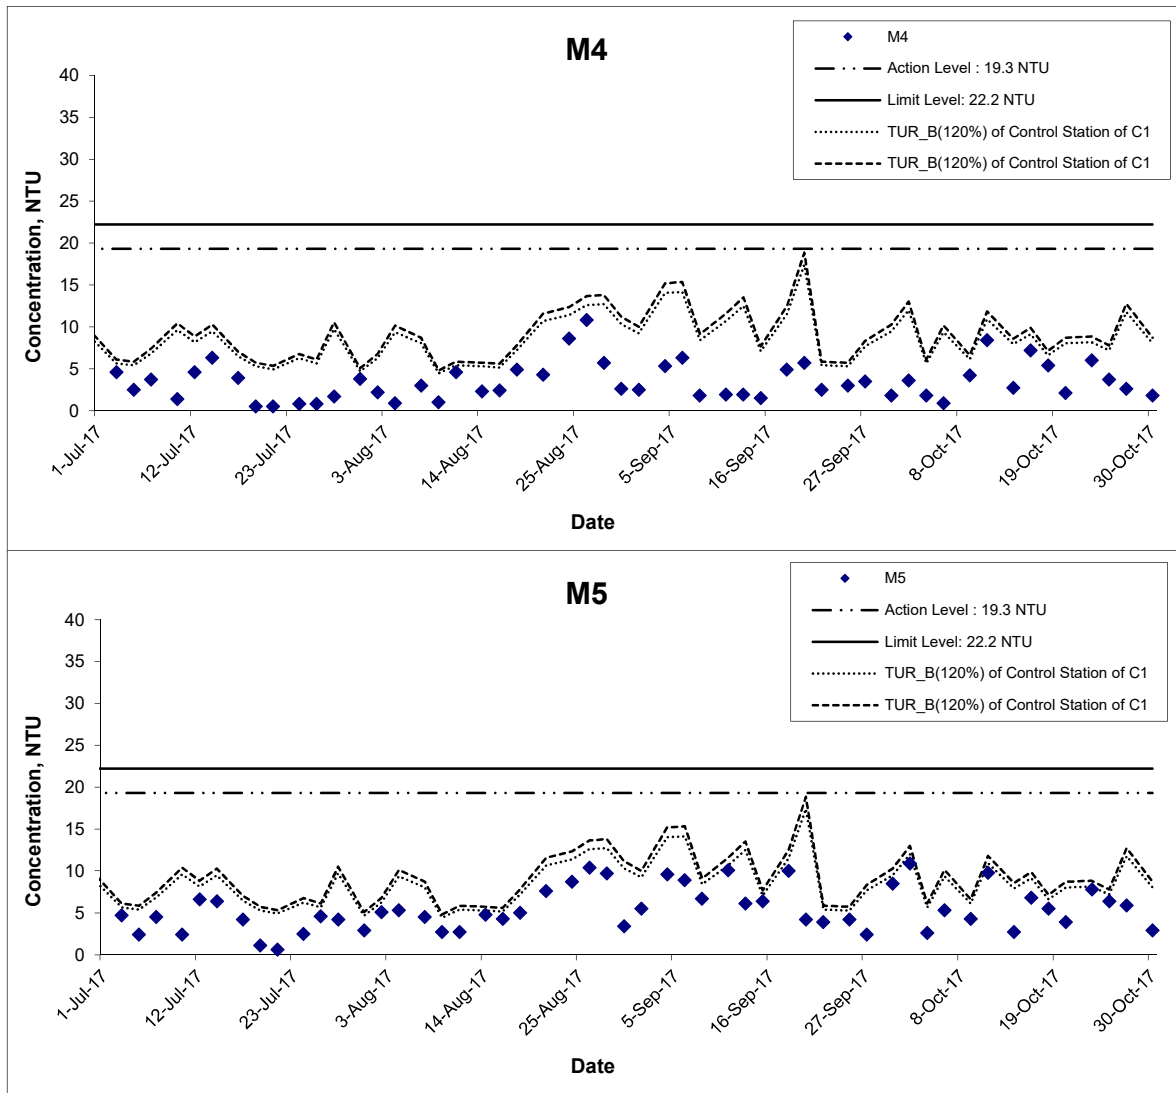


| | | | | | | |
|-------|--|-------|--------|-------------|---------|----------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Water Quality Monitoring Results | Date | Oct 17 | Appendix | I | |

Turbidity (Intake Level of WSD Salt Water Intake) at Mid-Ebb Tide

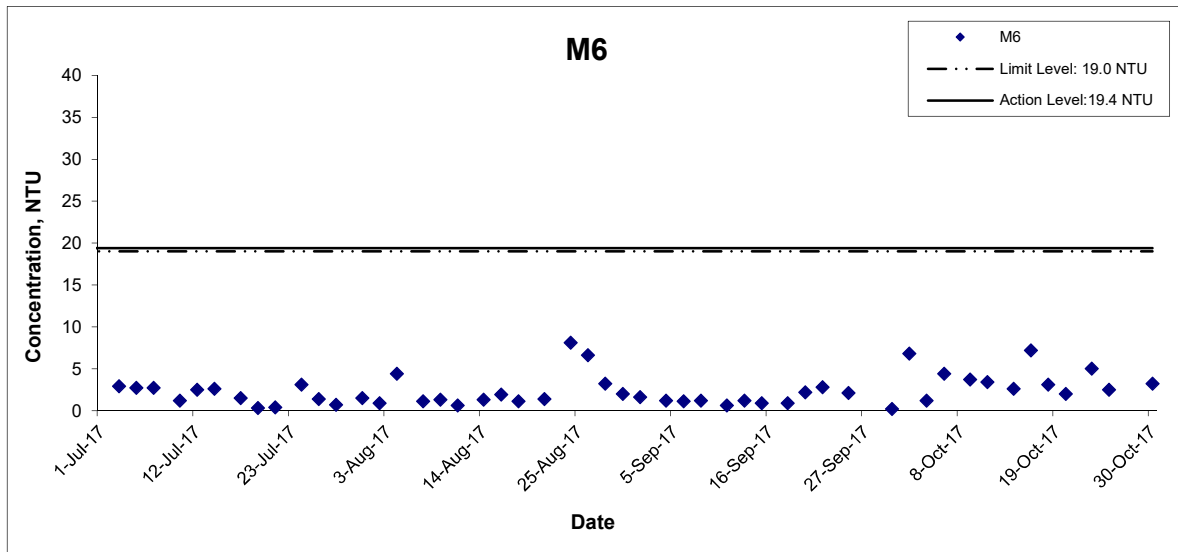


| | | | | | |
|---|-------|--------|-------------|---------|----------|
| Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Water Quality Monitoring Results | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Date | Oct 17 | Appendix | I | |

Turbidity (Intake Level of WSD Salt Water Intake) at Mid-Flood Tide

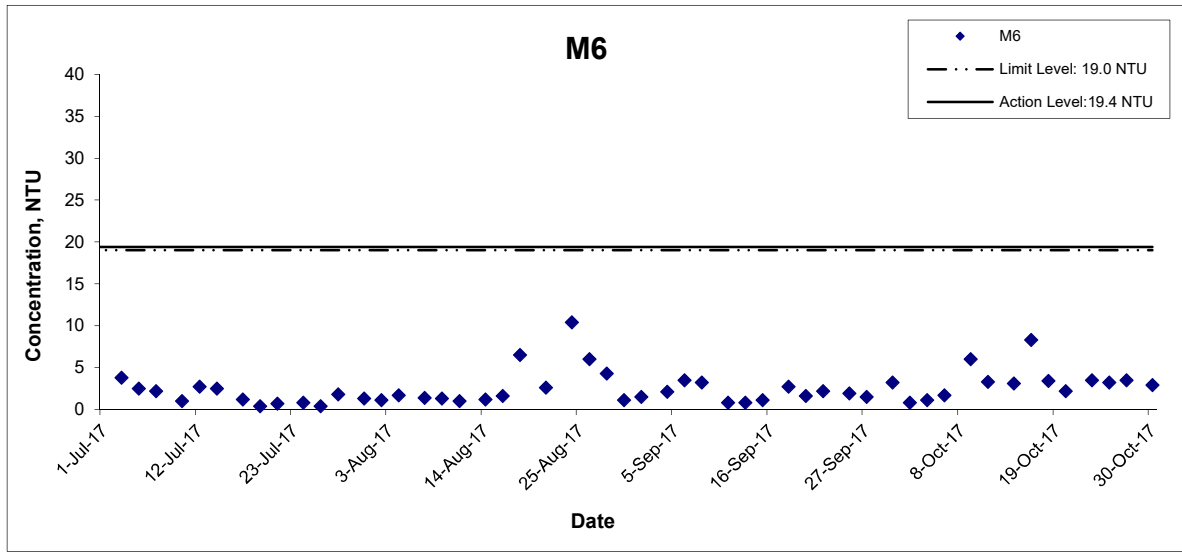

| | | | | | | |
|-------|--|-------|--------|-------------|---------|-----------------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Water Quality Monitoring Results | Date | Oct 17 | Appendix | I | |

Suspended Solids (Depth-averaged) at Mid-Ebb Tide

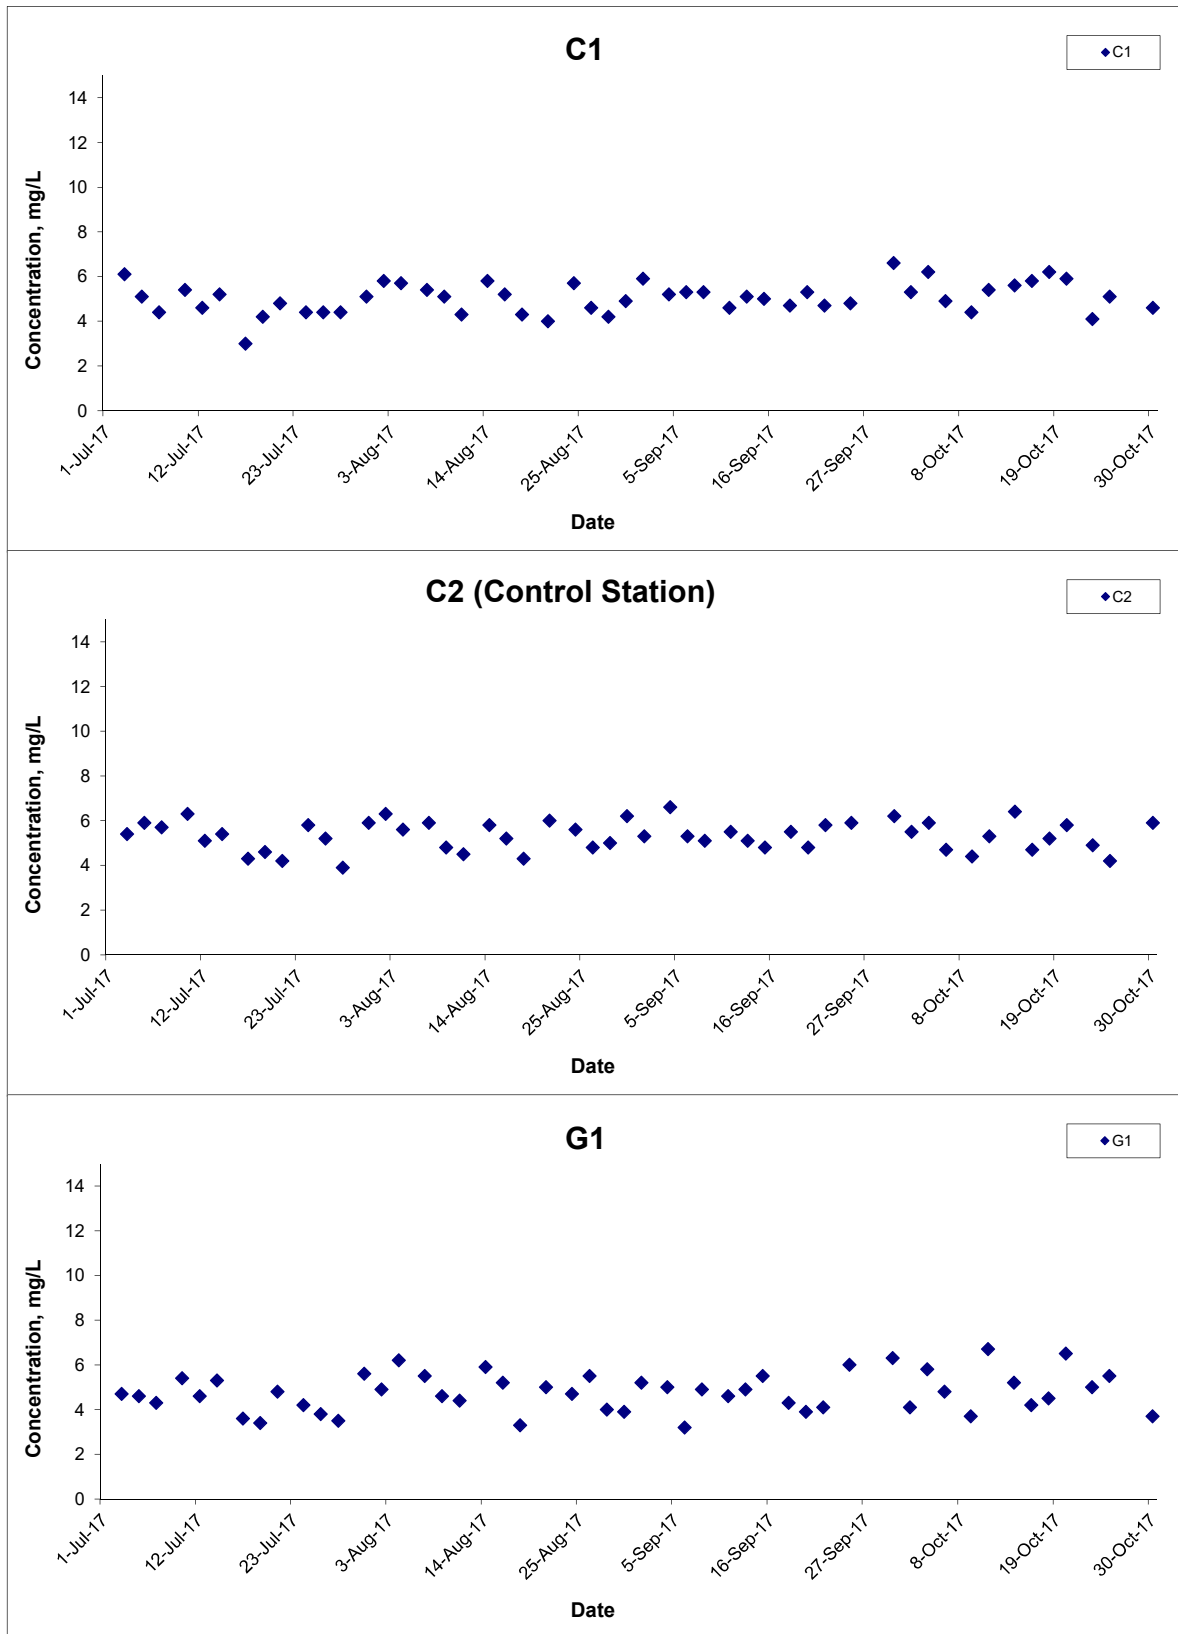


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I



Suspended Solids (Depth-averaged) at Mid-Ebb Tide

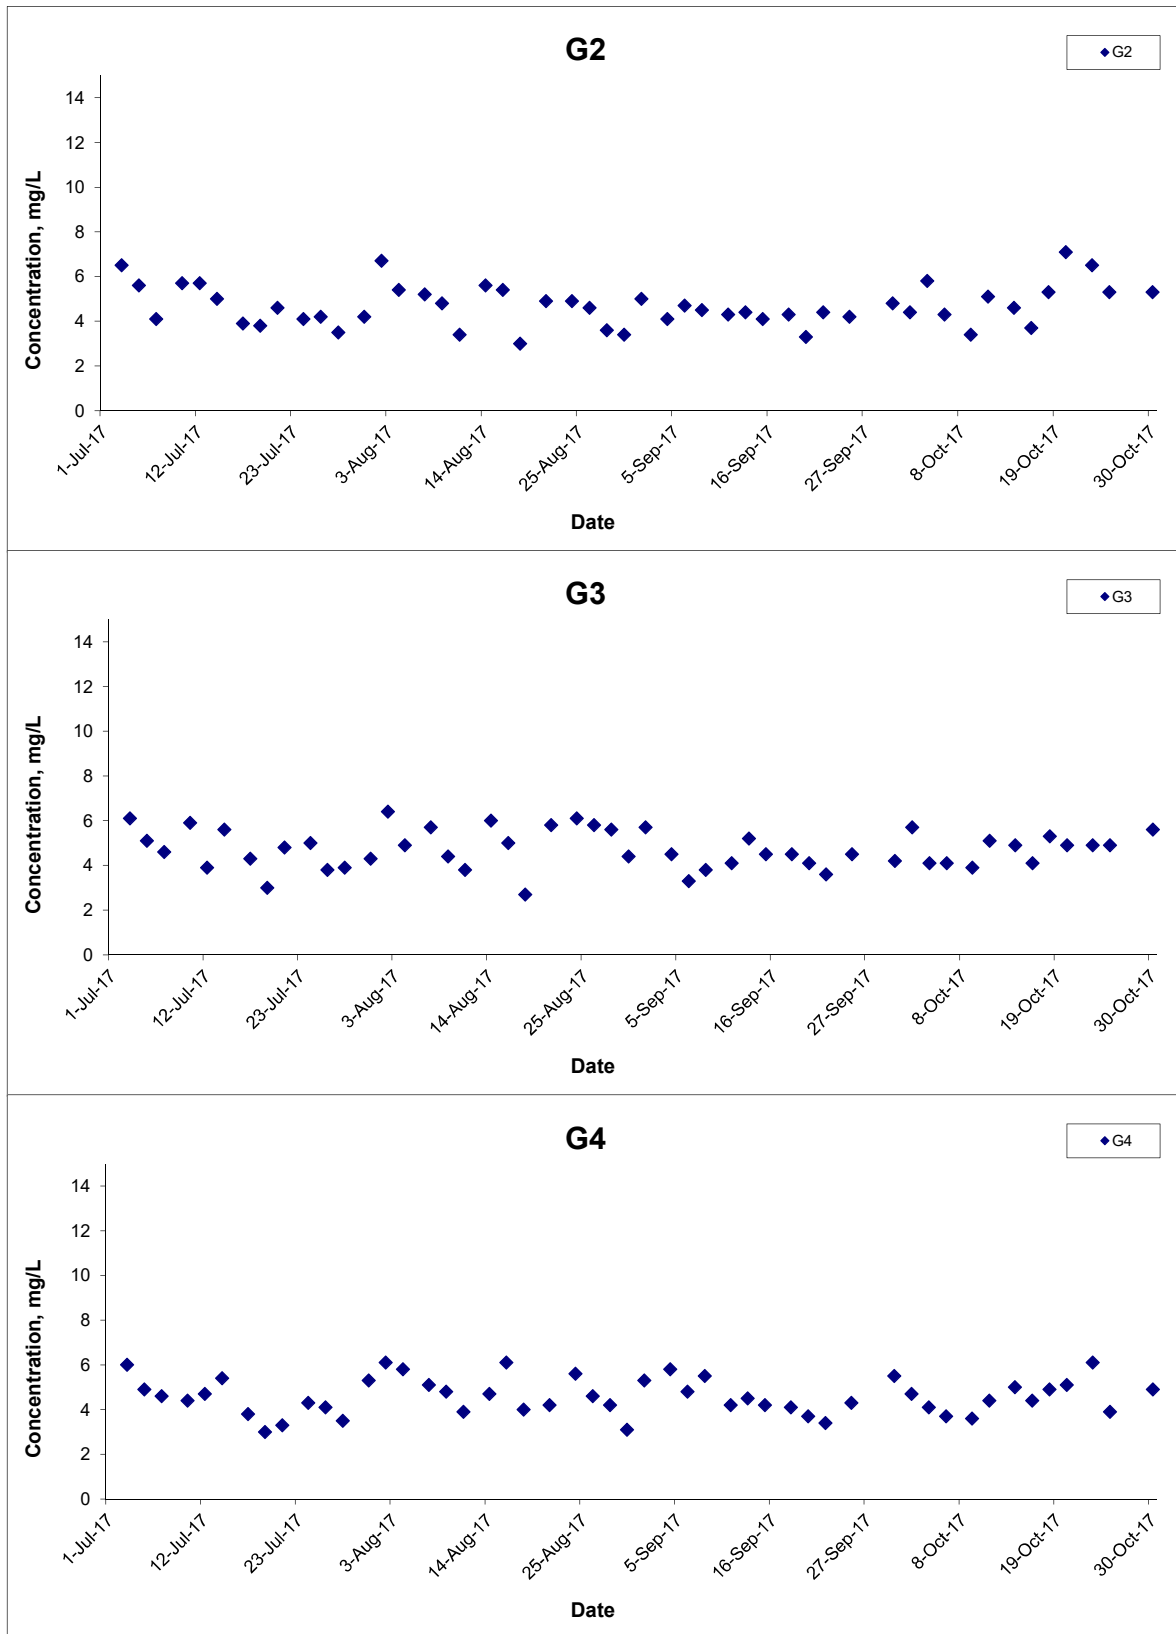

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Depth-averaged) at Mid-Ebb Tide

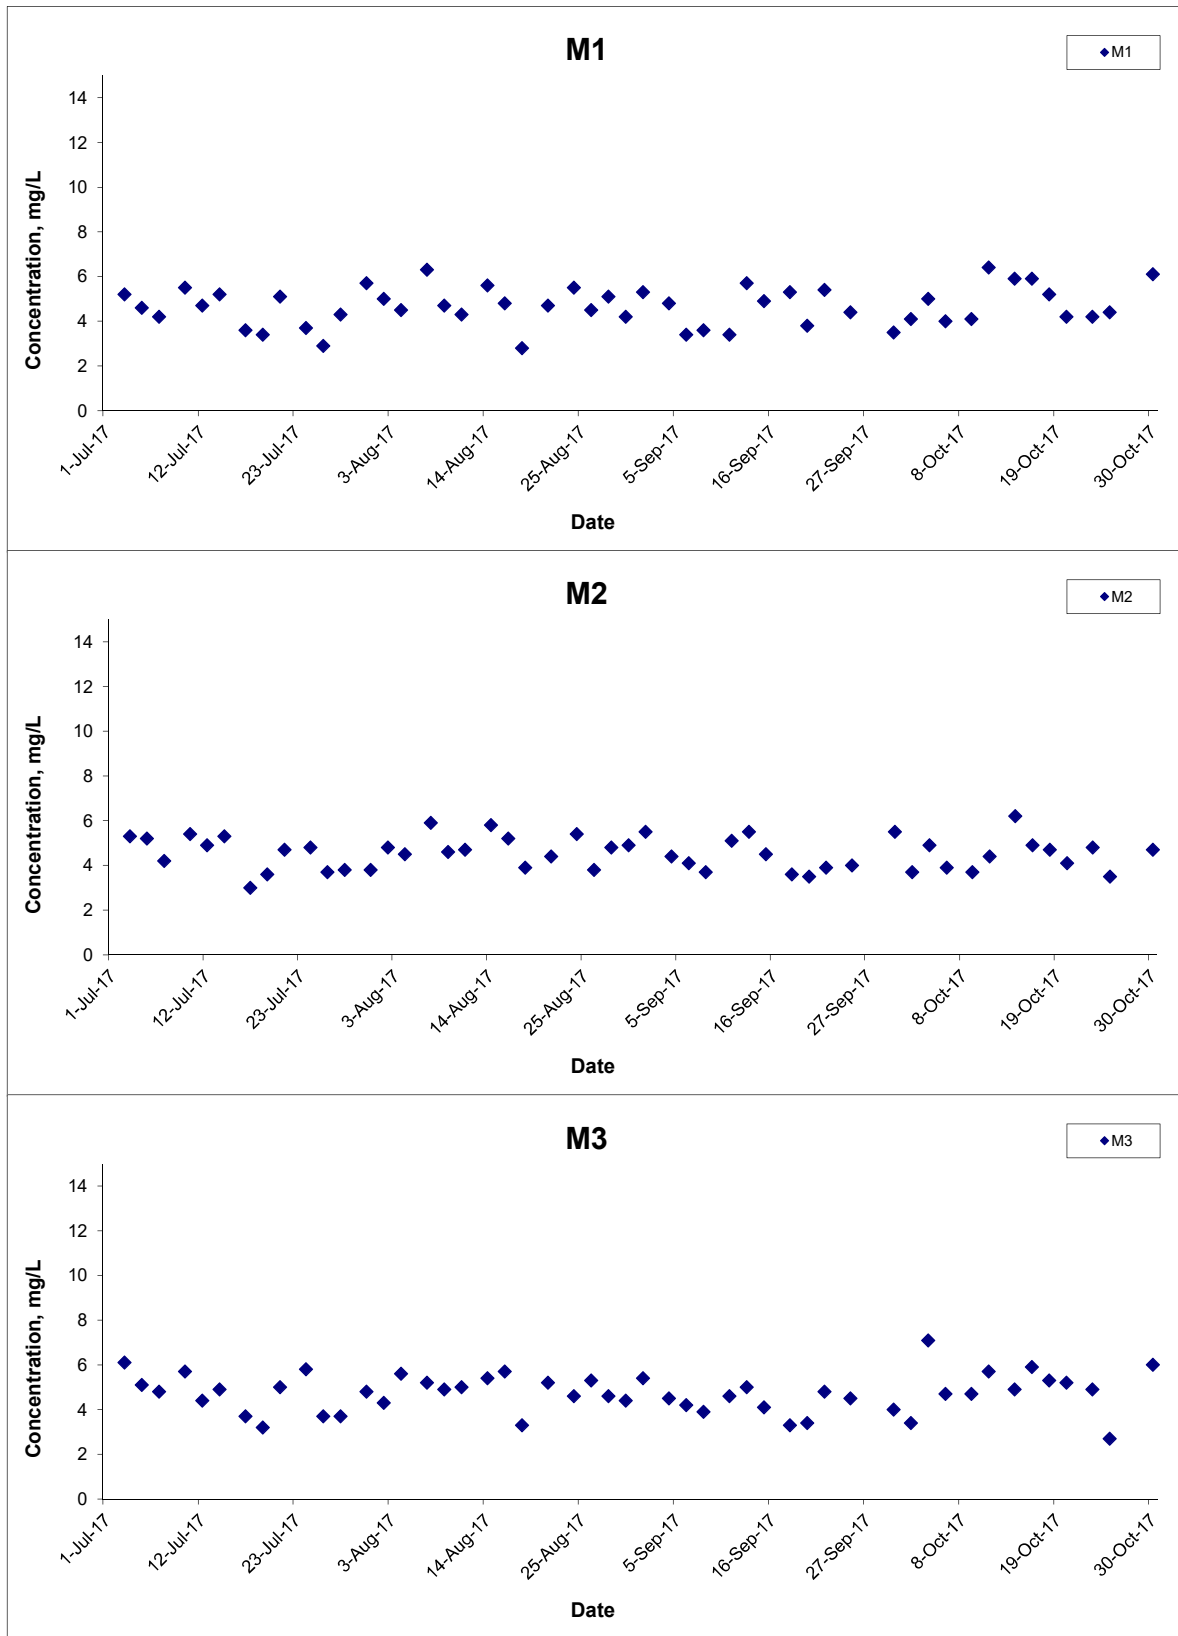

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I




Suspended Solids (Depth-averaged) at Mid-Ebb Tide

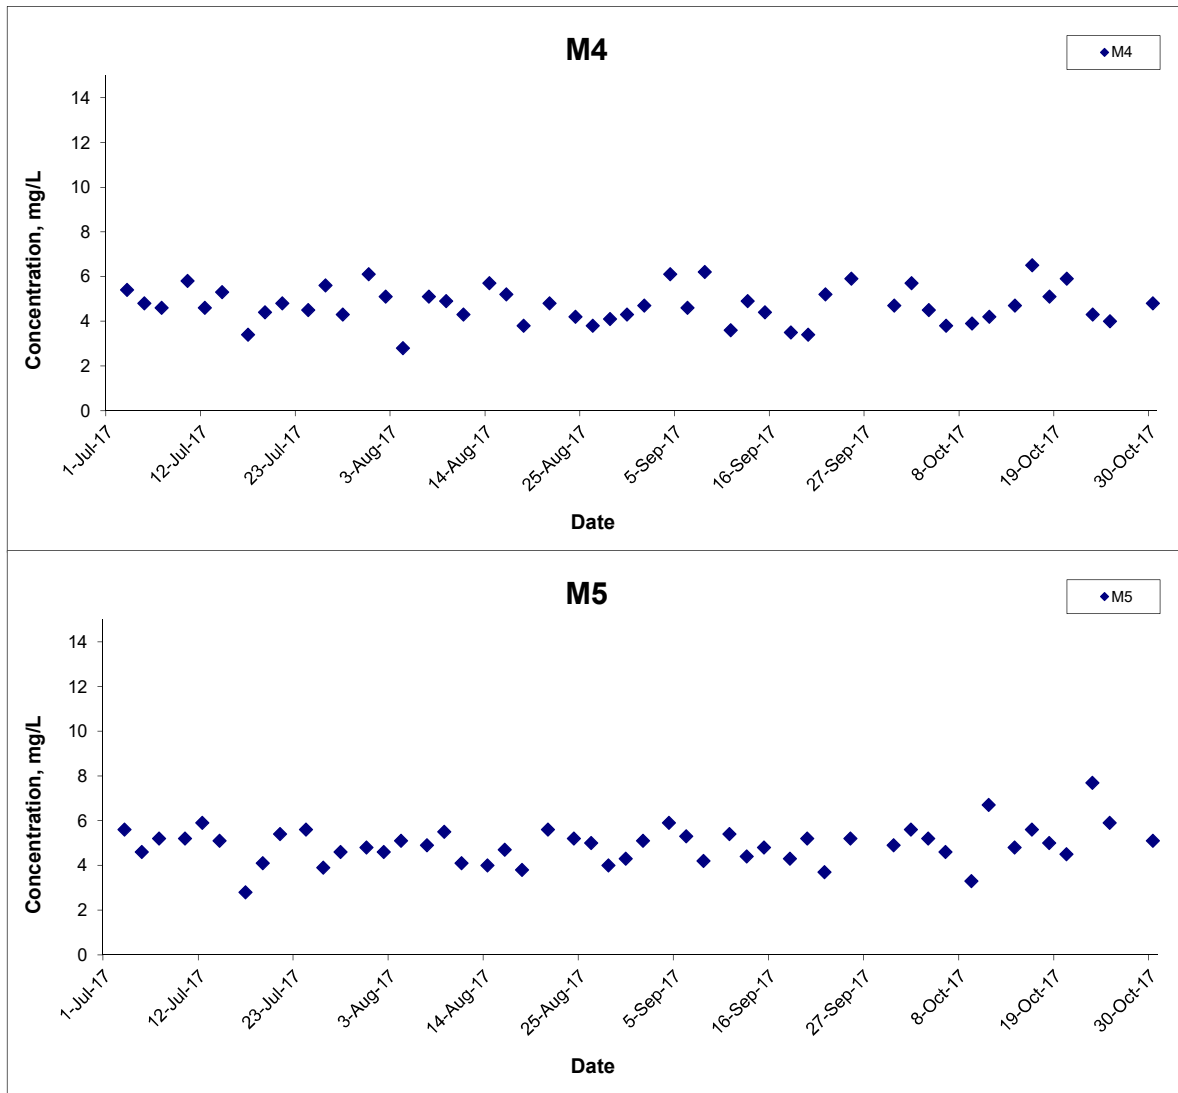

| | | | |
|---|----------------|------------------------|----------|
| Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Water Quality Monitoring Results | Scale N.T.S | Project No. MA16034 | CINOTECH |
| | Date Oct 17 | Appendix I | |

Suspended Solids (Depth-averaged) at Mid-Flood Tide

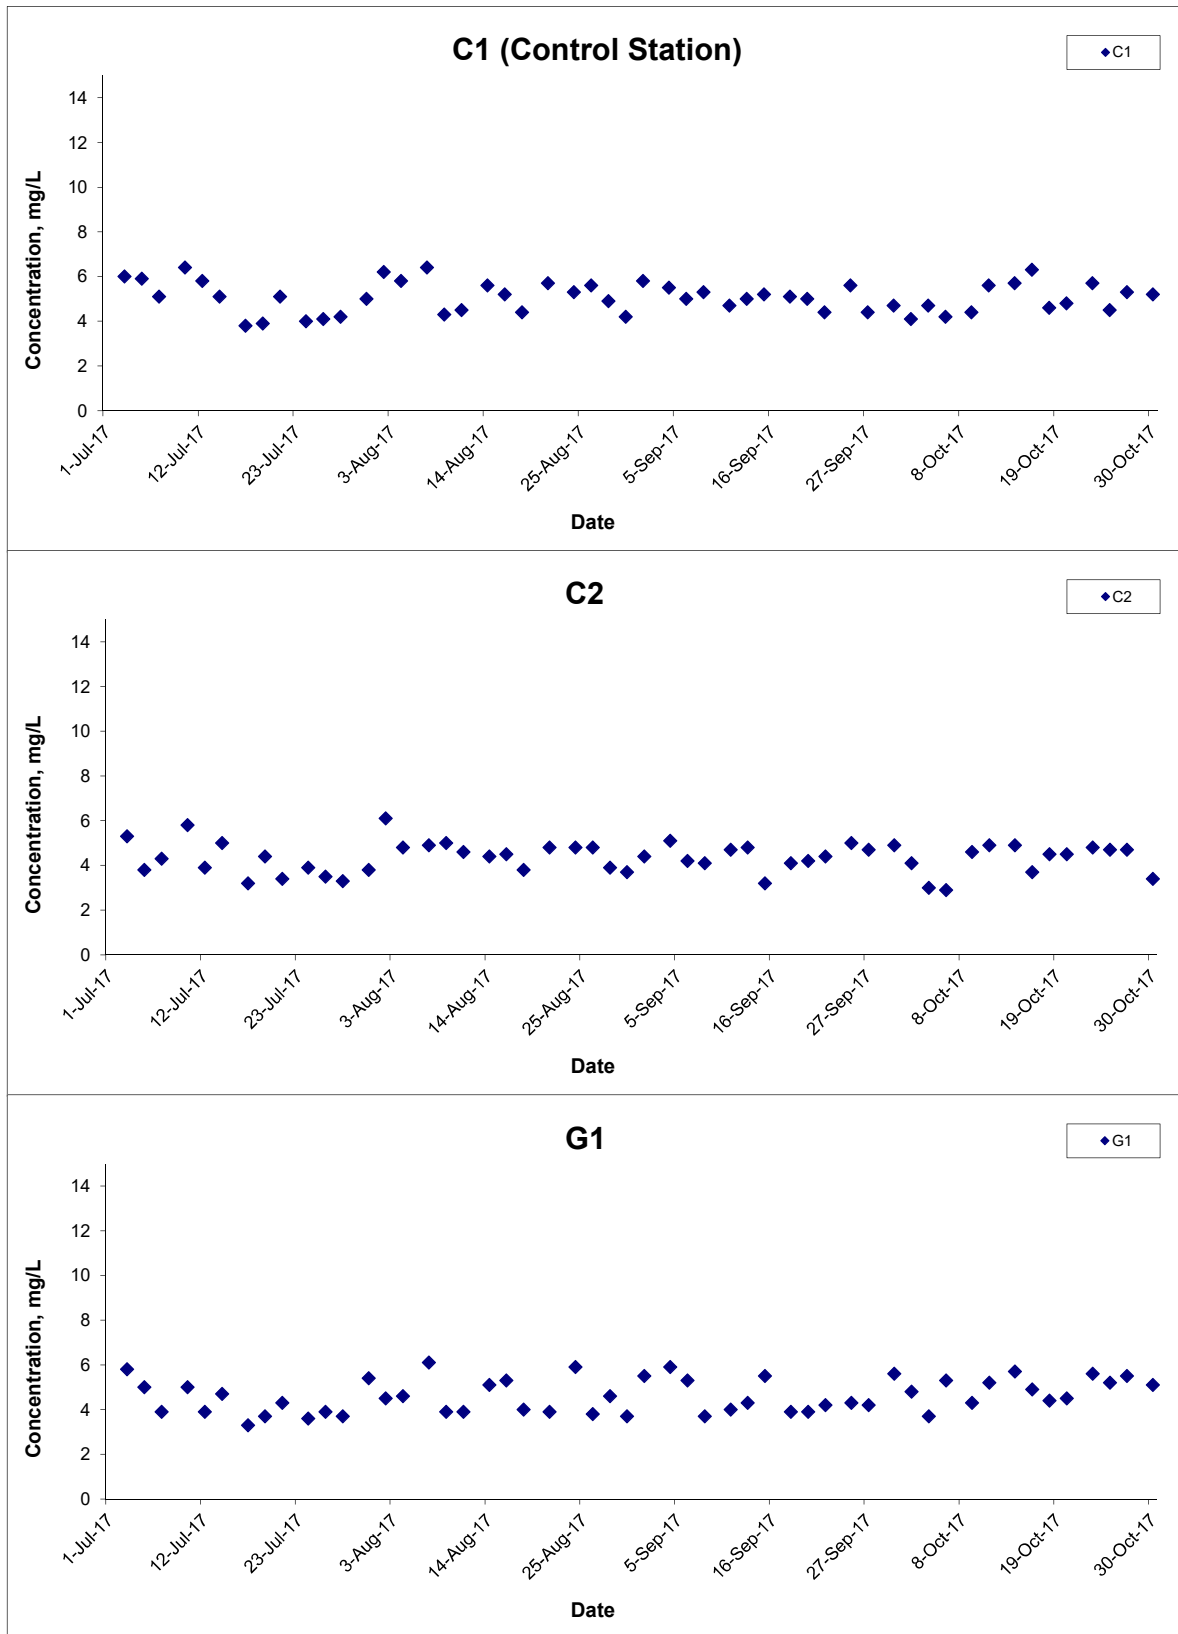

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Depth-averaged) at Mid-Flood Tide

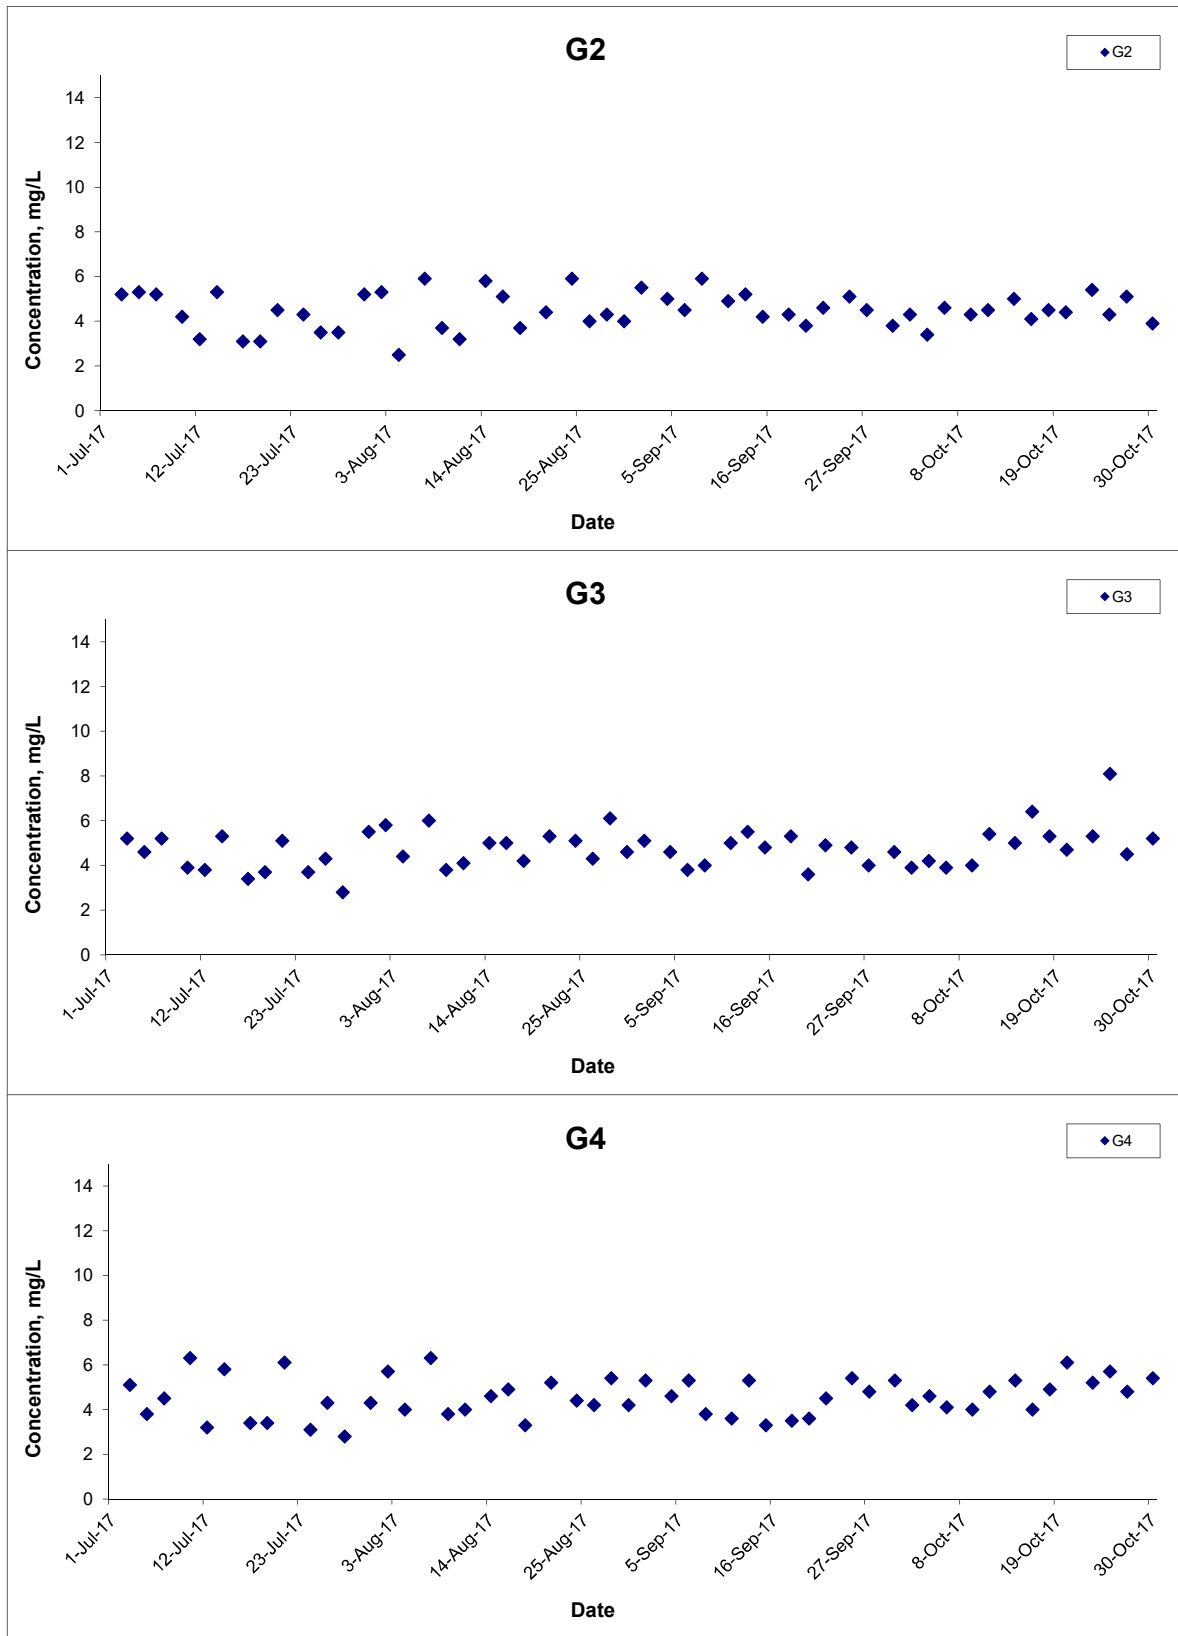

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Depth-averaged) at Mid-Flood Tide

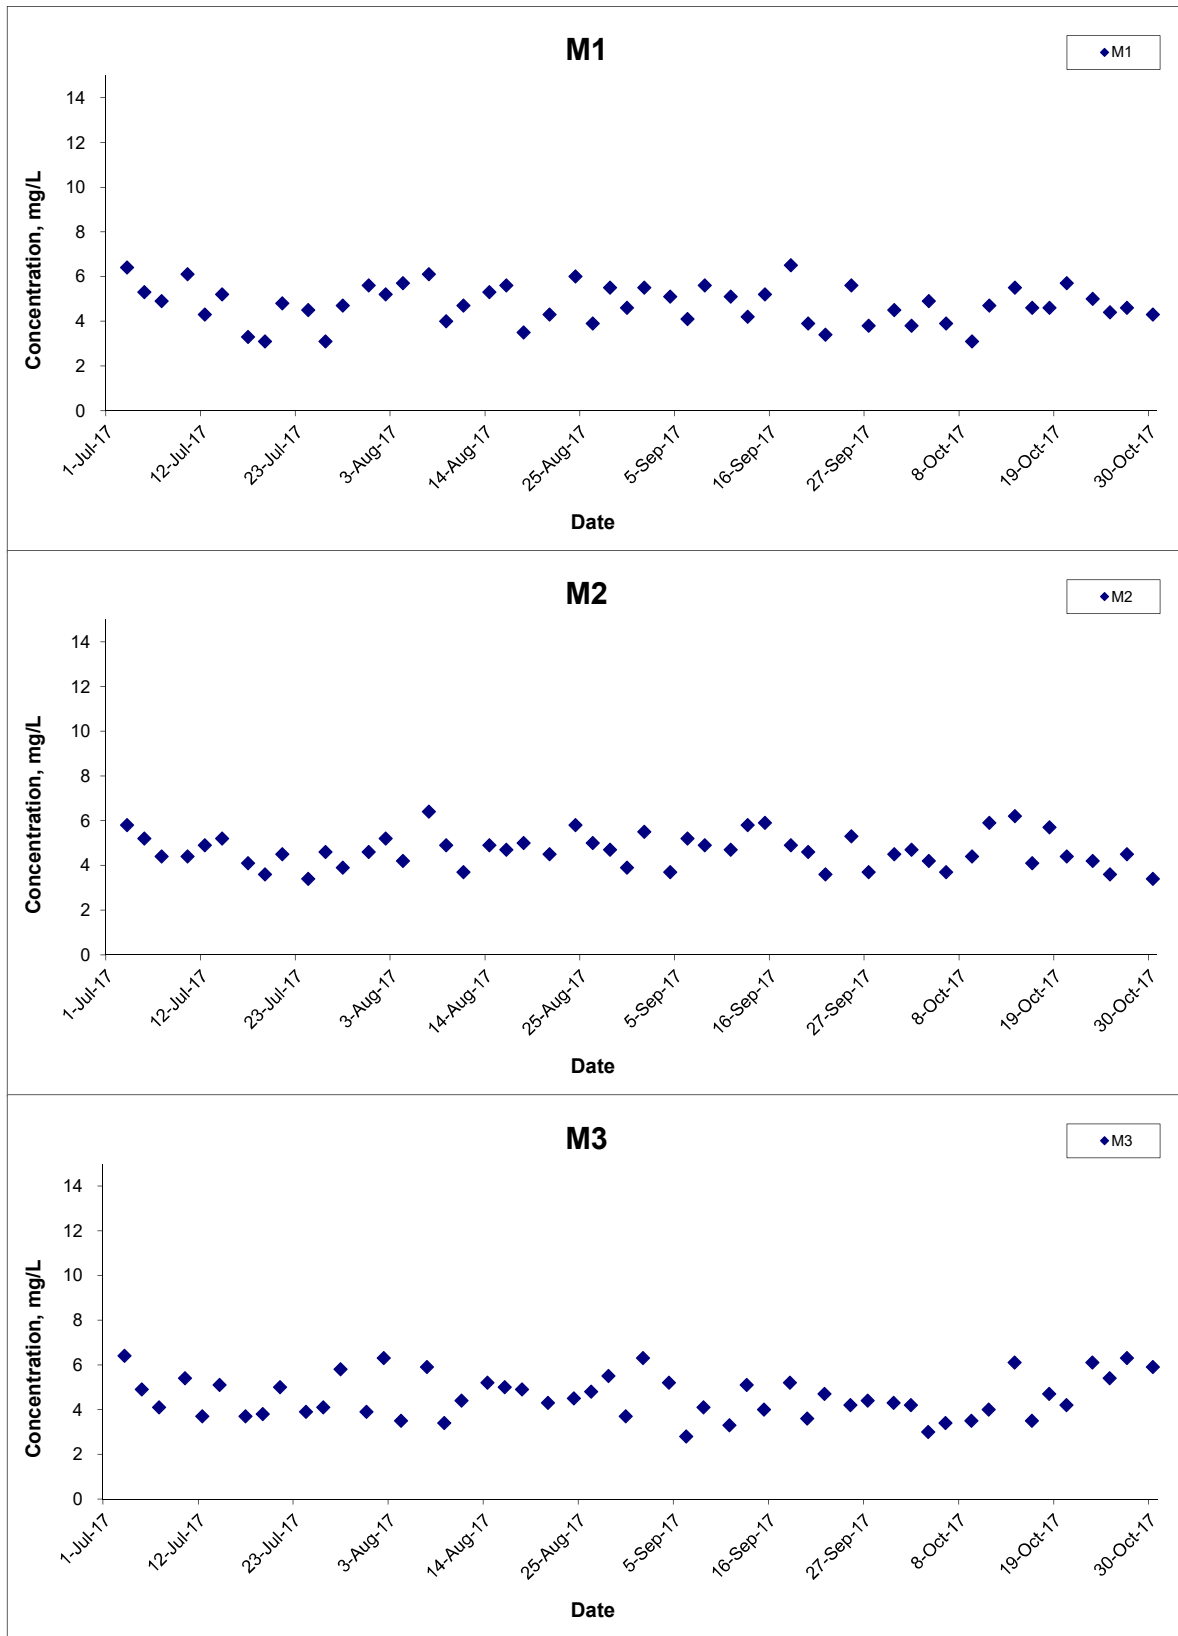


Title
 Agreement No. CE 59/2015(EP) Environmental Team for
 Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring
 Results

Scale
 N.T.S
Date
 Oct 17

Project No.
 MA16034
Appendix
 I




Suspended Solids (Depth-averaged) at Mid-Flood Tide

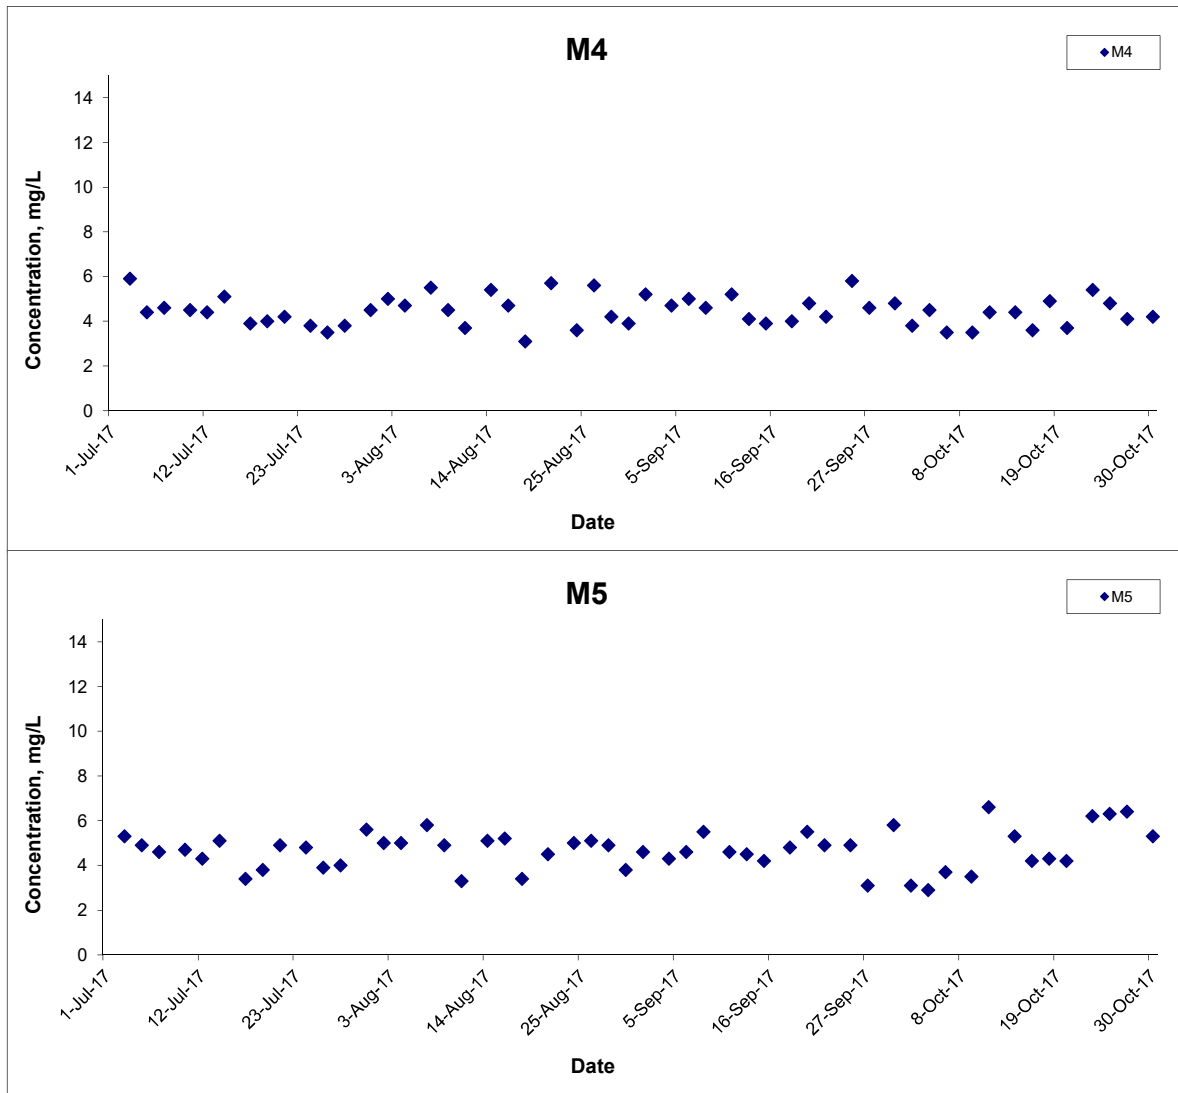

| | | | |
|---|----------------|------------------------|----------|
| Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Water Quality Monitoring Results | Scale N.T.S | Project No. MA16034 | CINOTECH |
| | Date Oct 17 | Appendix I | |

Suspended Solids (Surface) at Mid-Ebb Tide

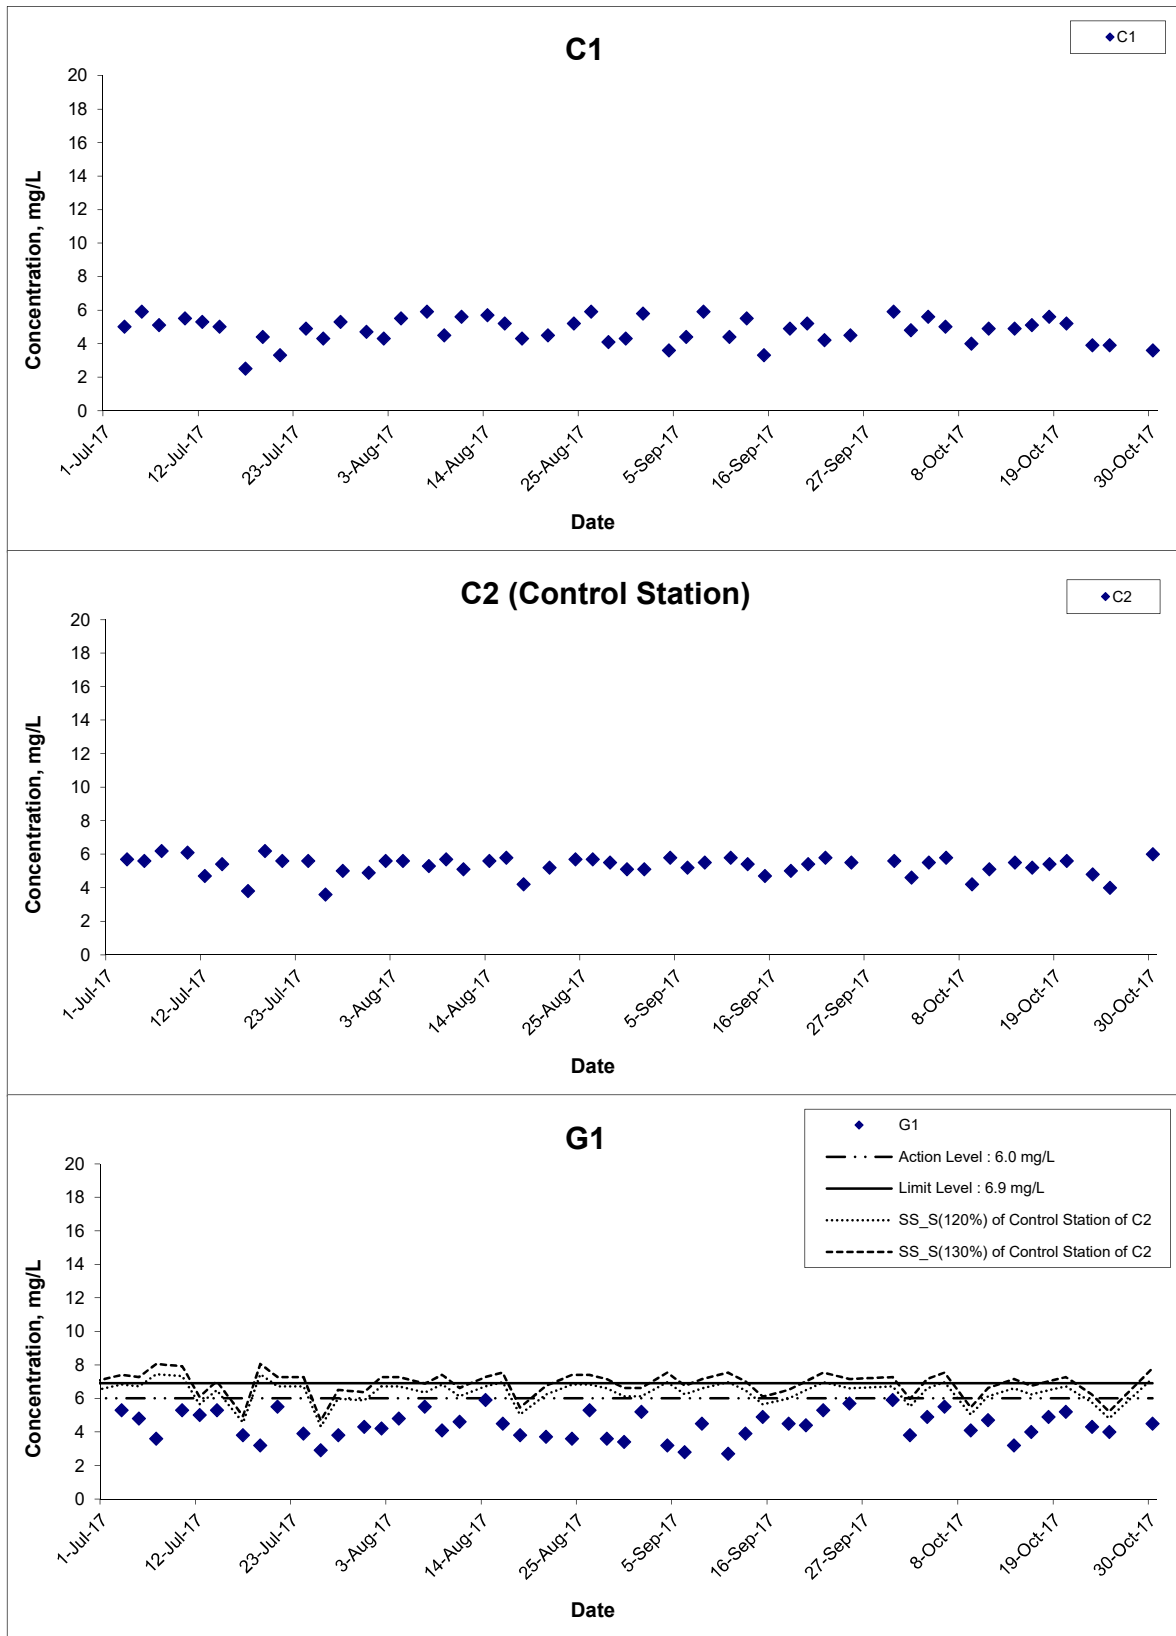

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I




Suspended Solids (Surface) at Mid-Ebb Tide

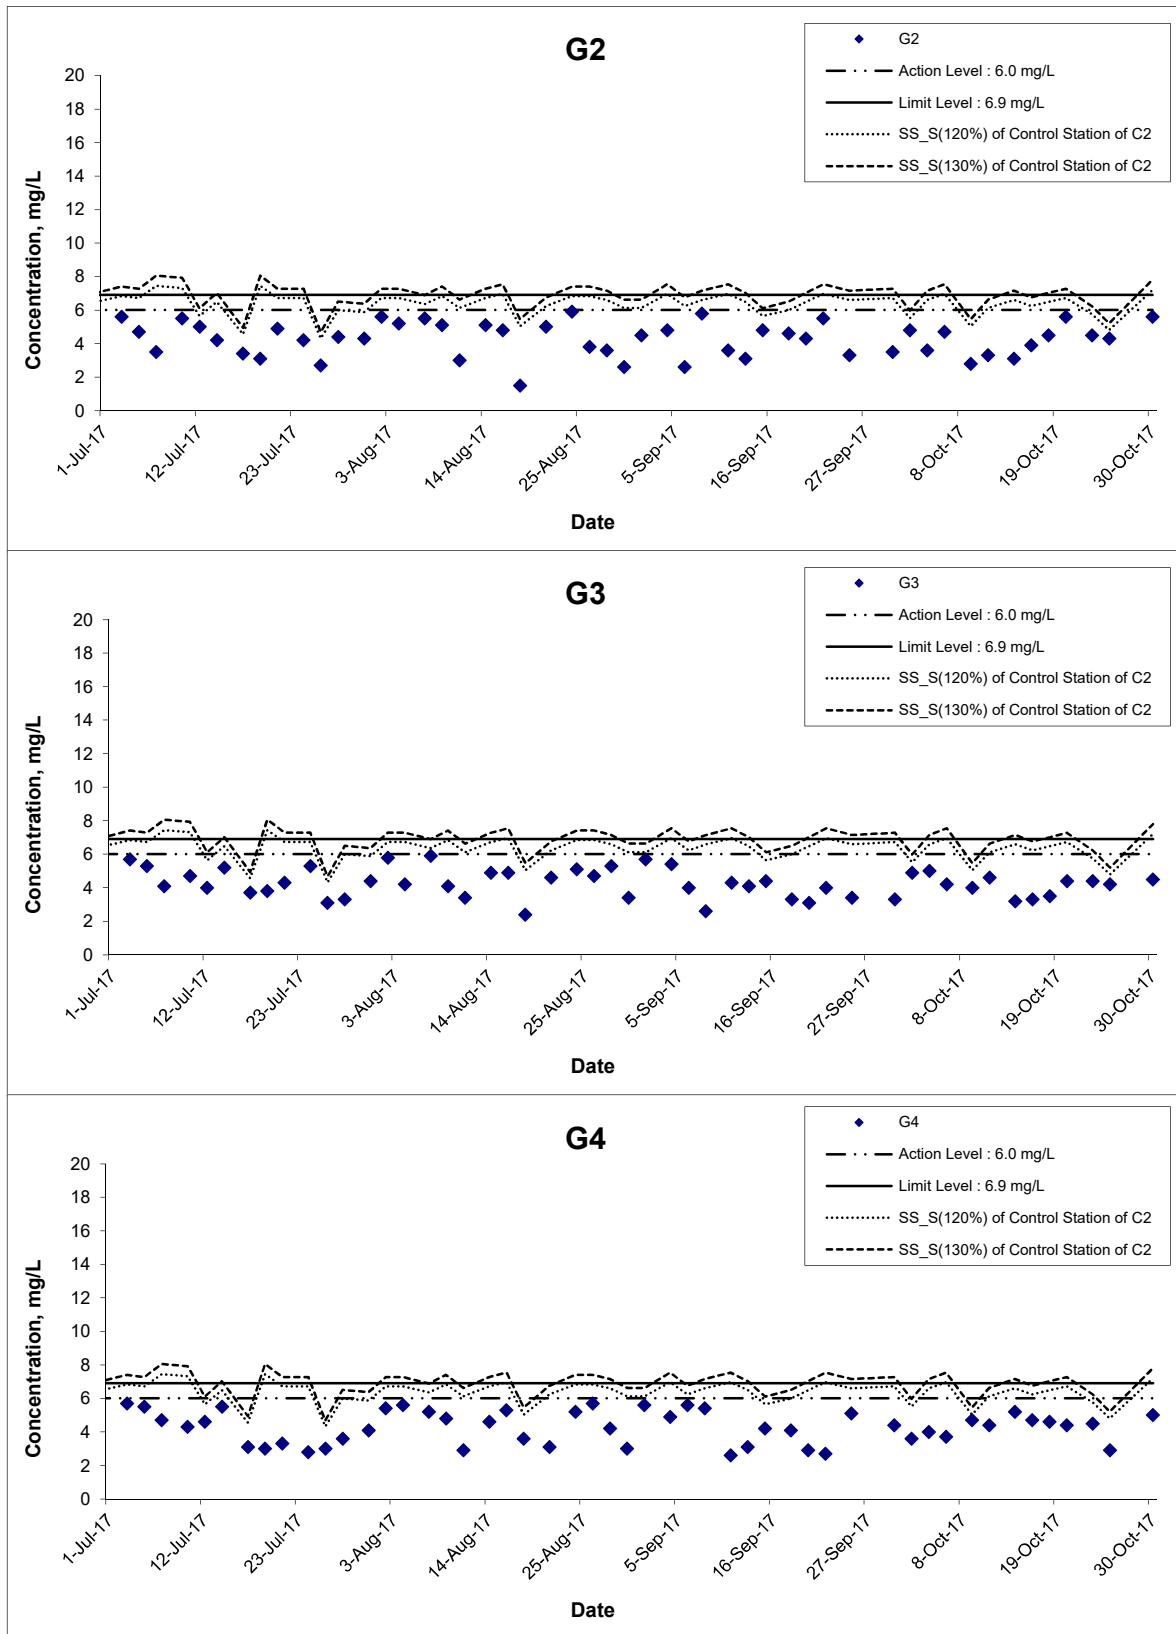

Remarks: The graphical point at zero concentration is presented as <2.5mg/L.

| | | | | |
|---|-------|--------|------------------------|-----------------|
| Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Water Quality Monitoring Results | Scale | N.T.S | Project No. MA16034 | CINOTECH |
| | Date | Oct 17 | Appendix I | |

Suspended Solids (Surface) at Mid-Ebb Tide

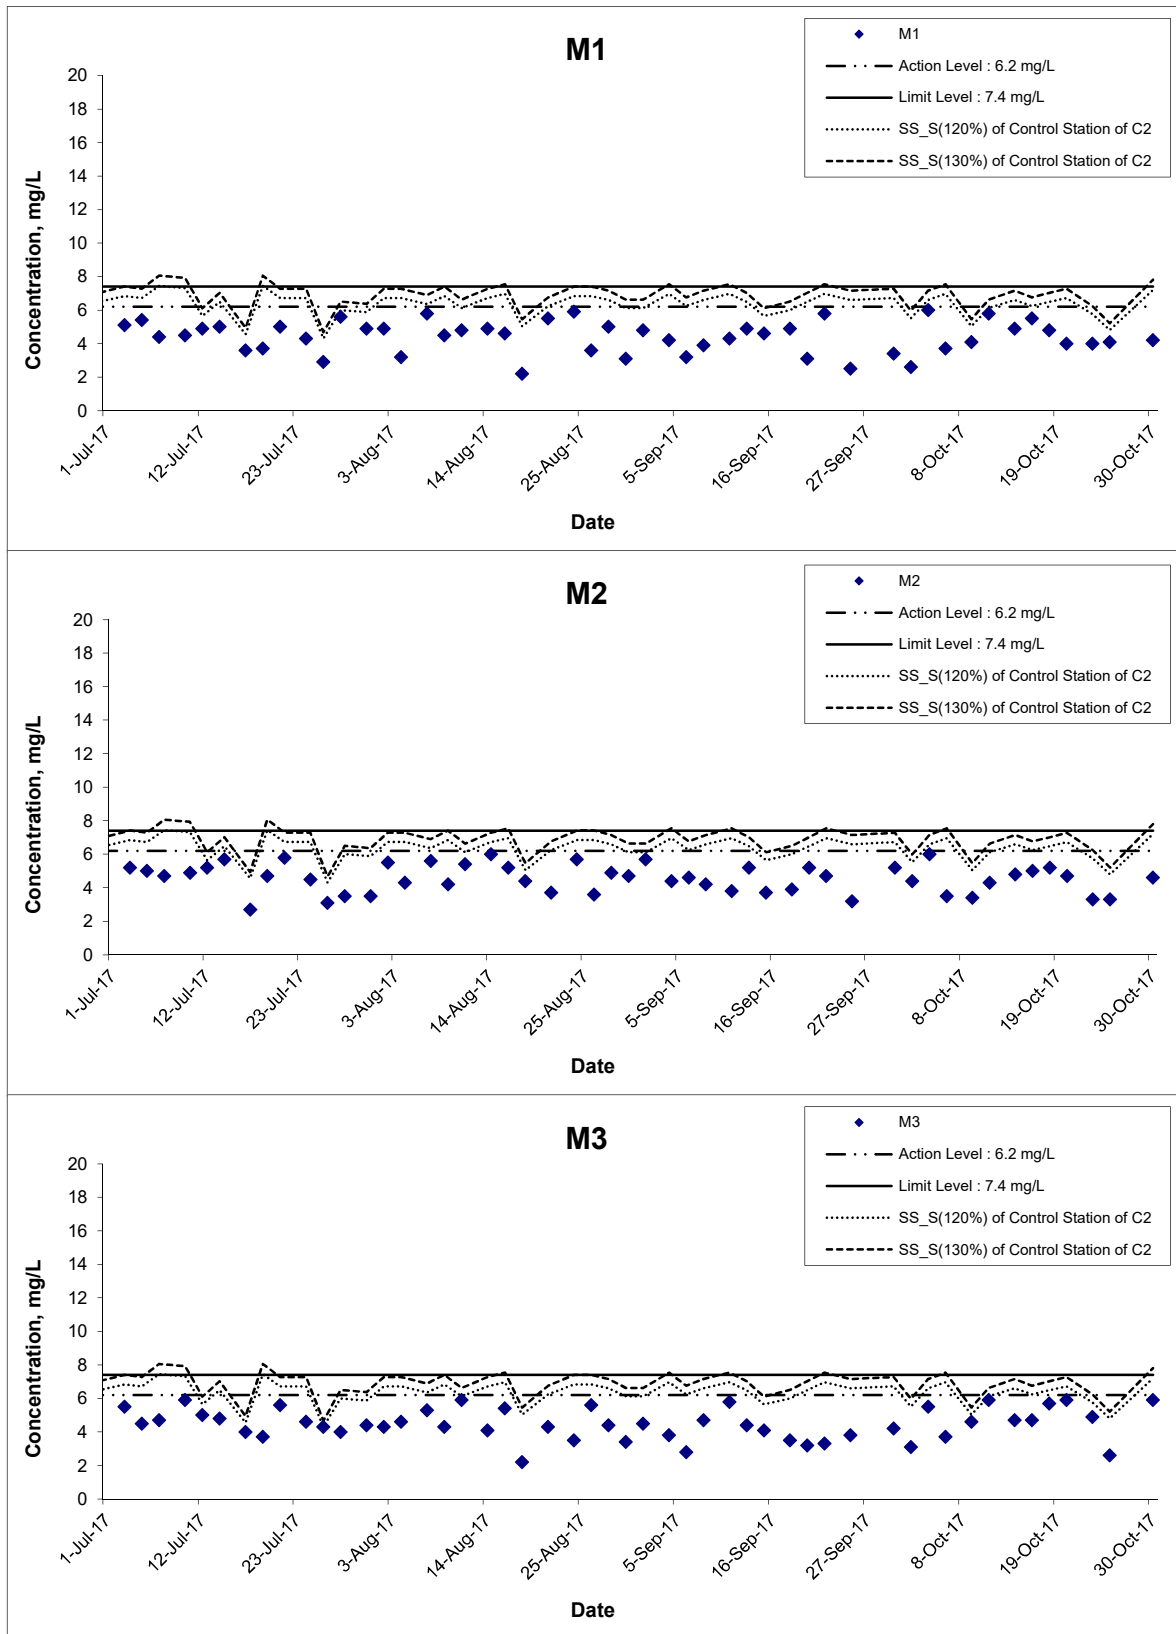

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Ebb Tide

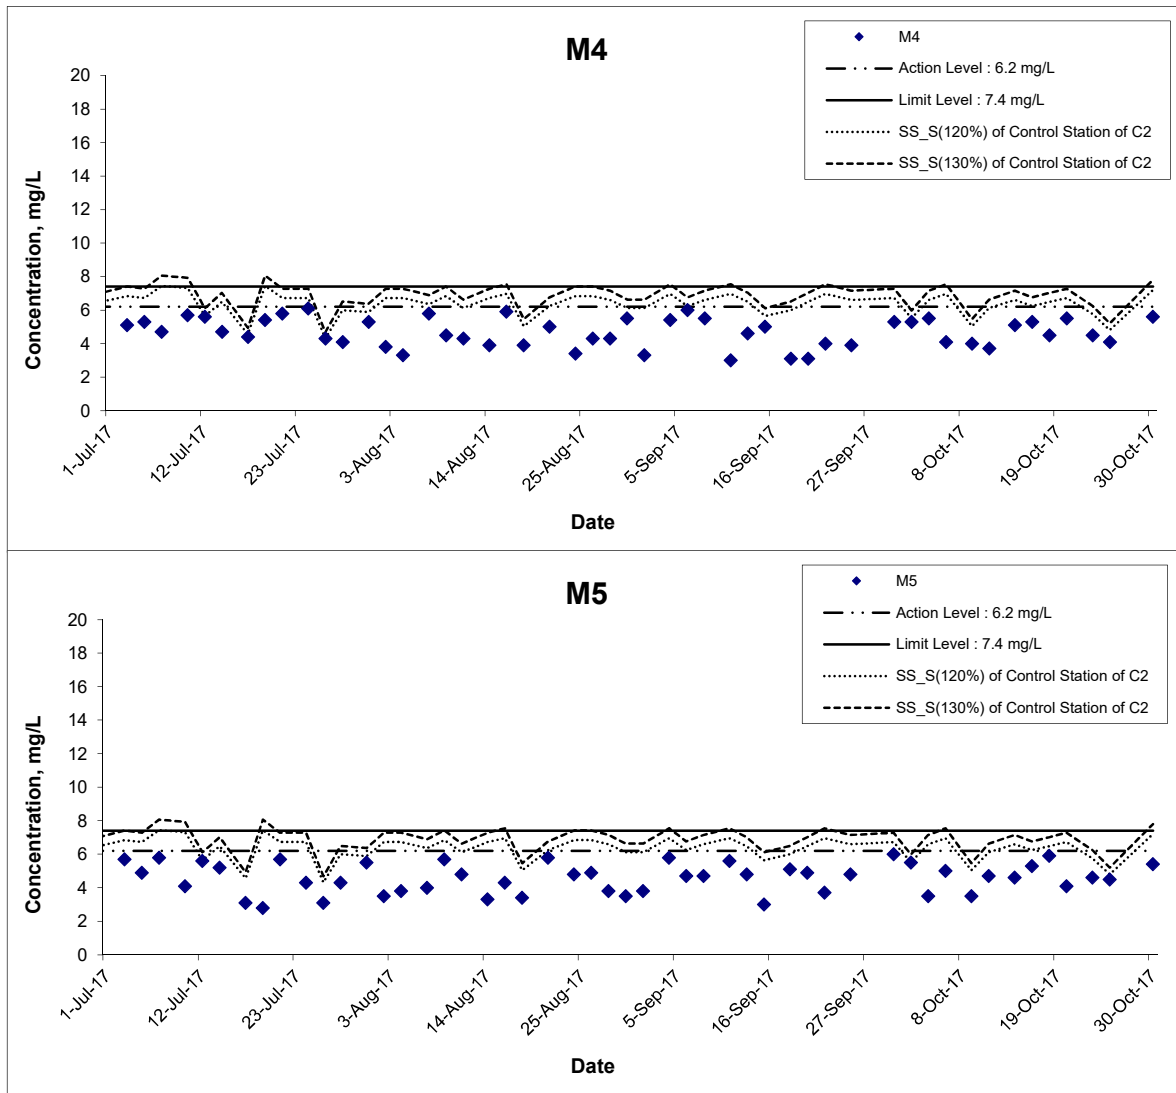

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Flood Tide

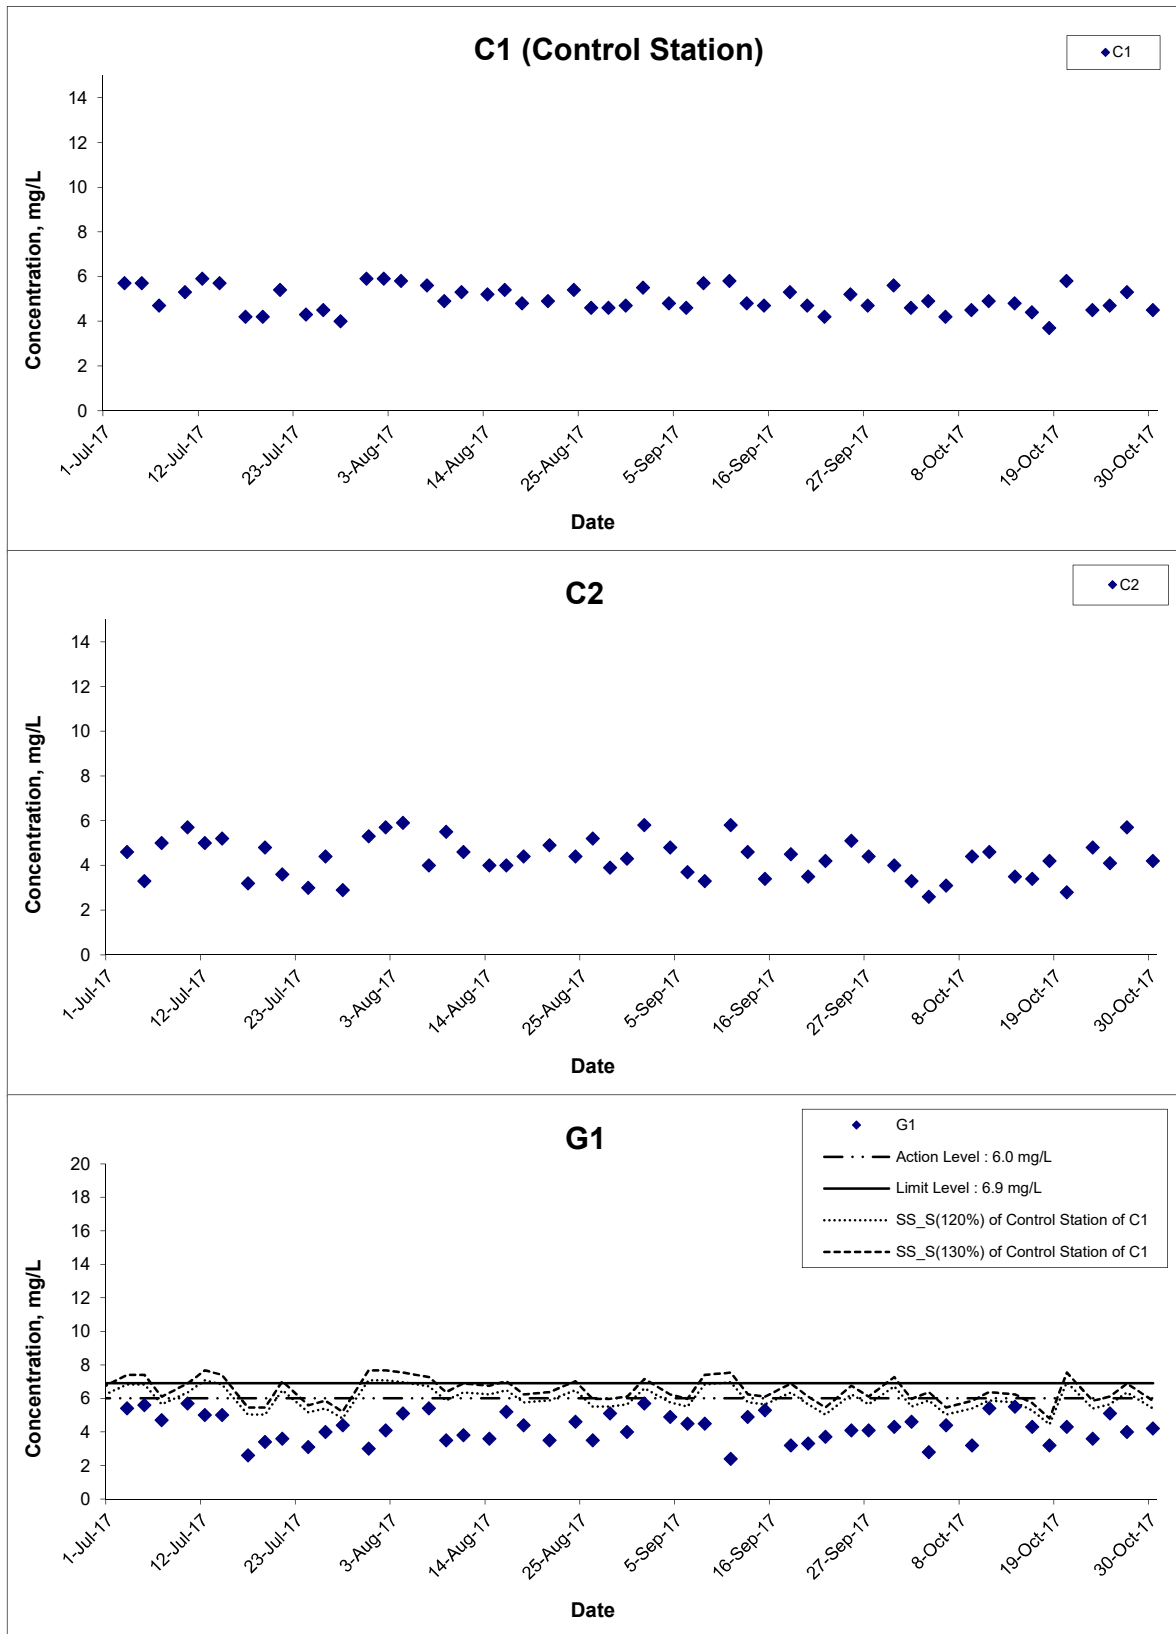

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Flood Tide

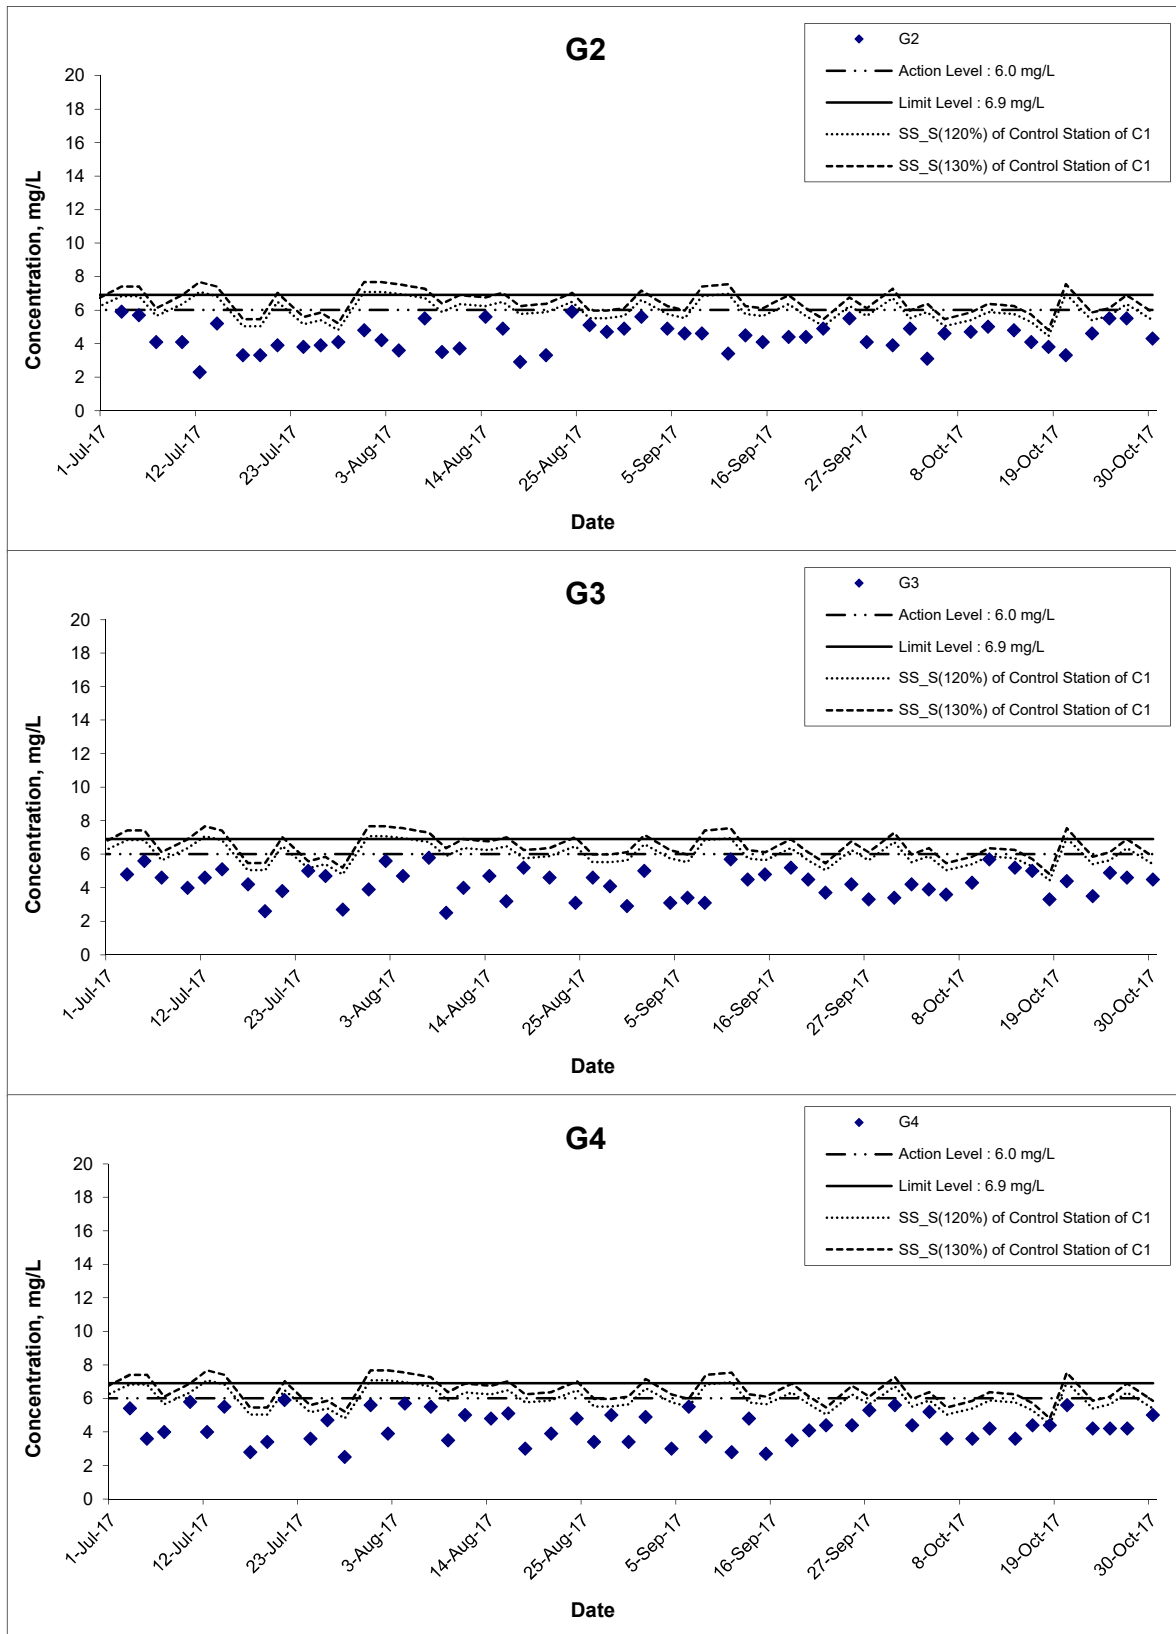

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Flood Tide

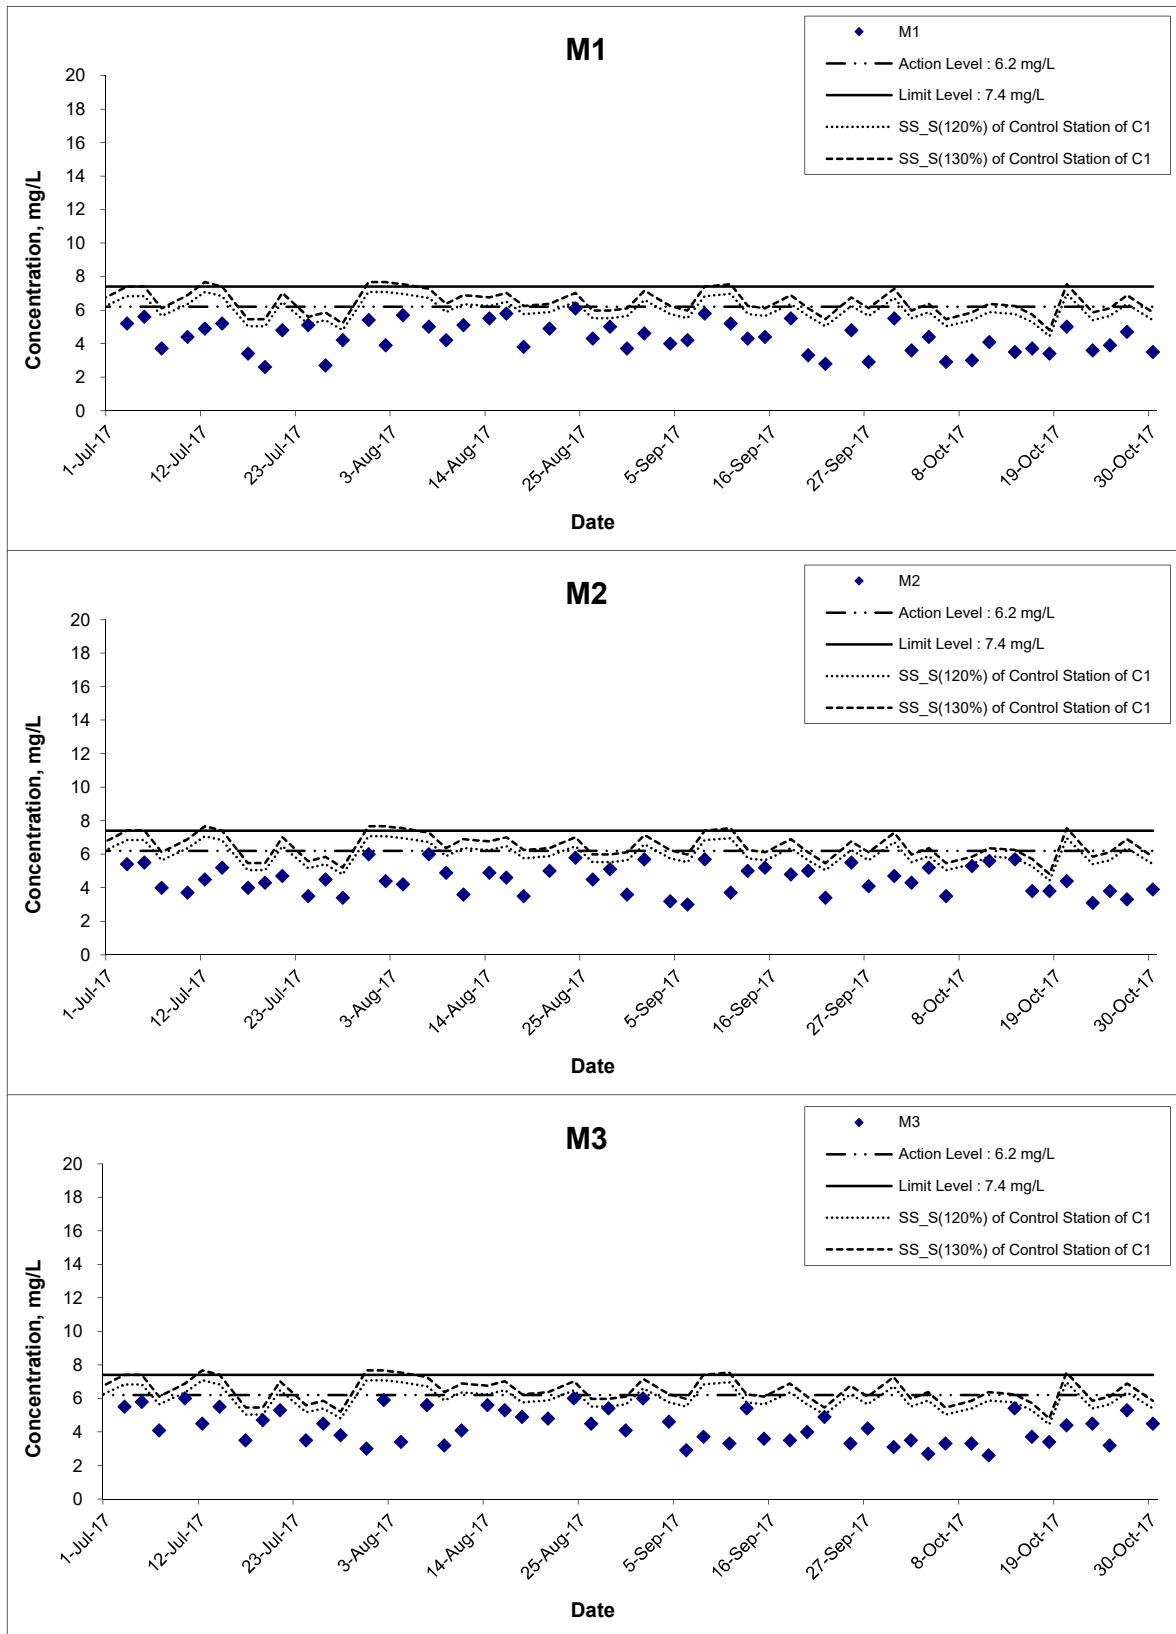

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Flood Tide

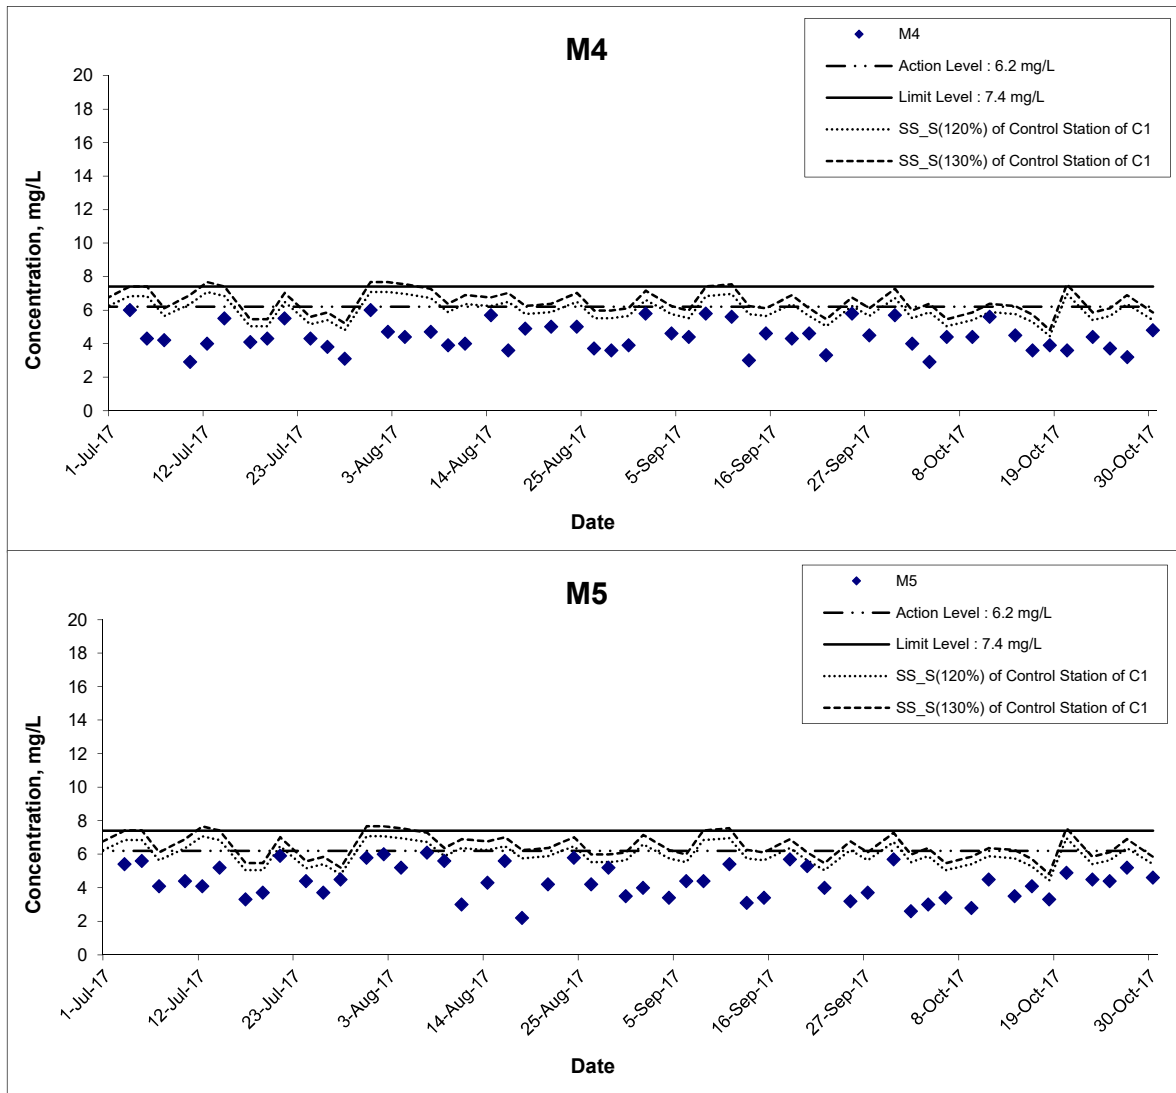

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Ebb Tide

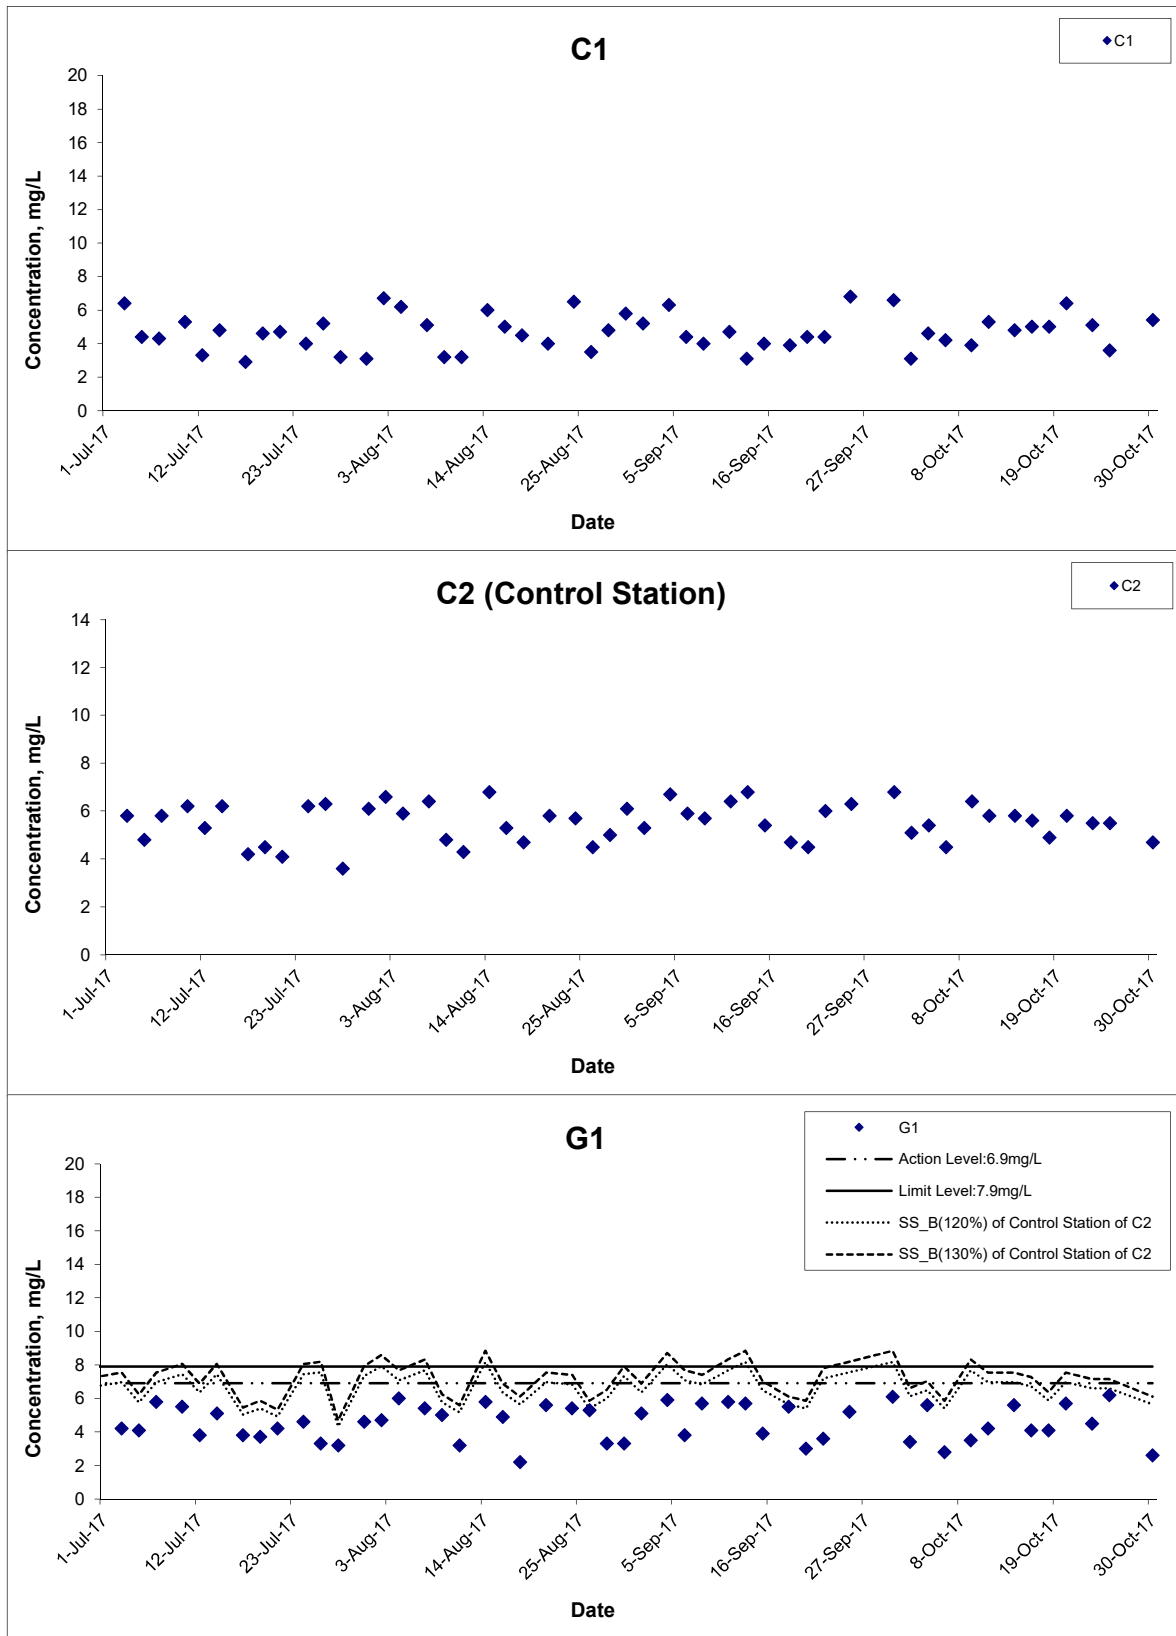

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Ebb Tide

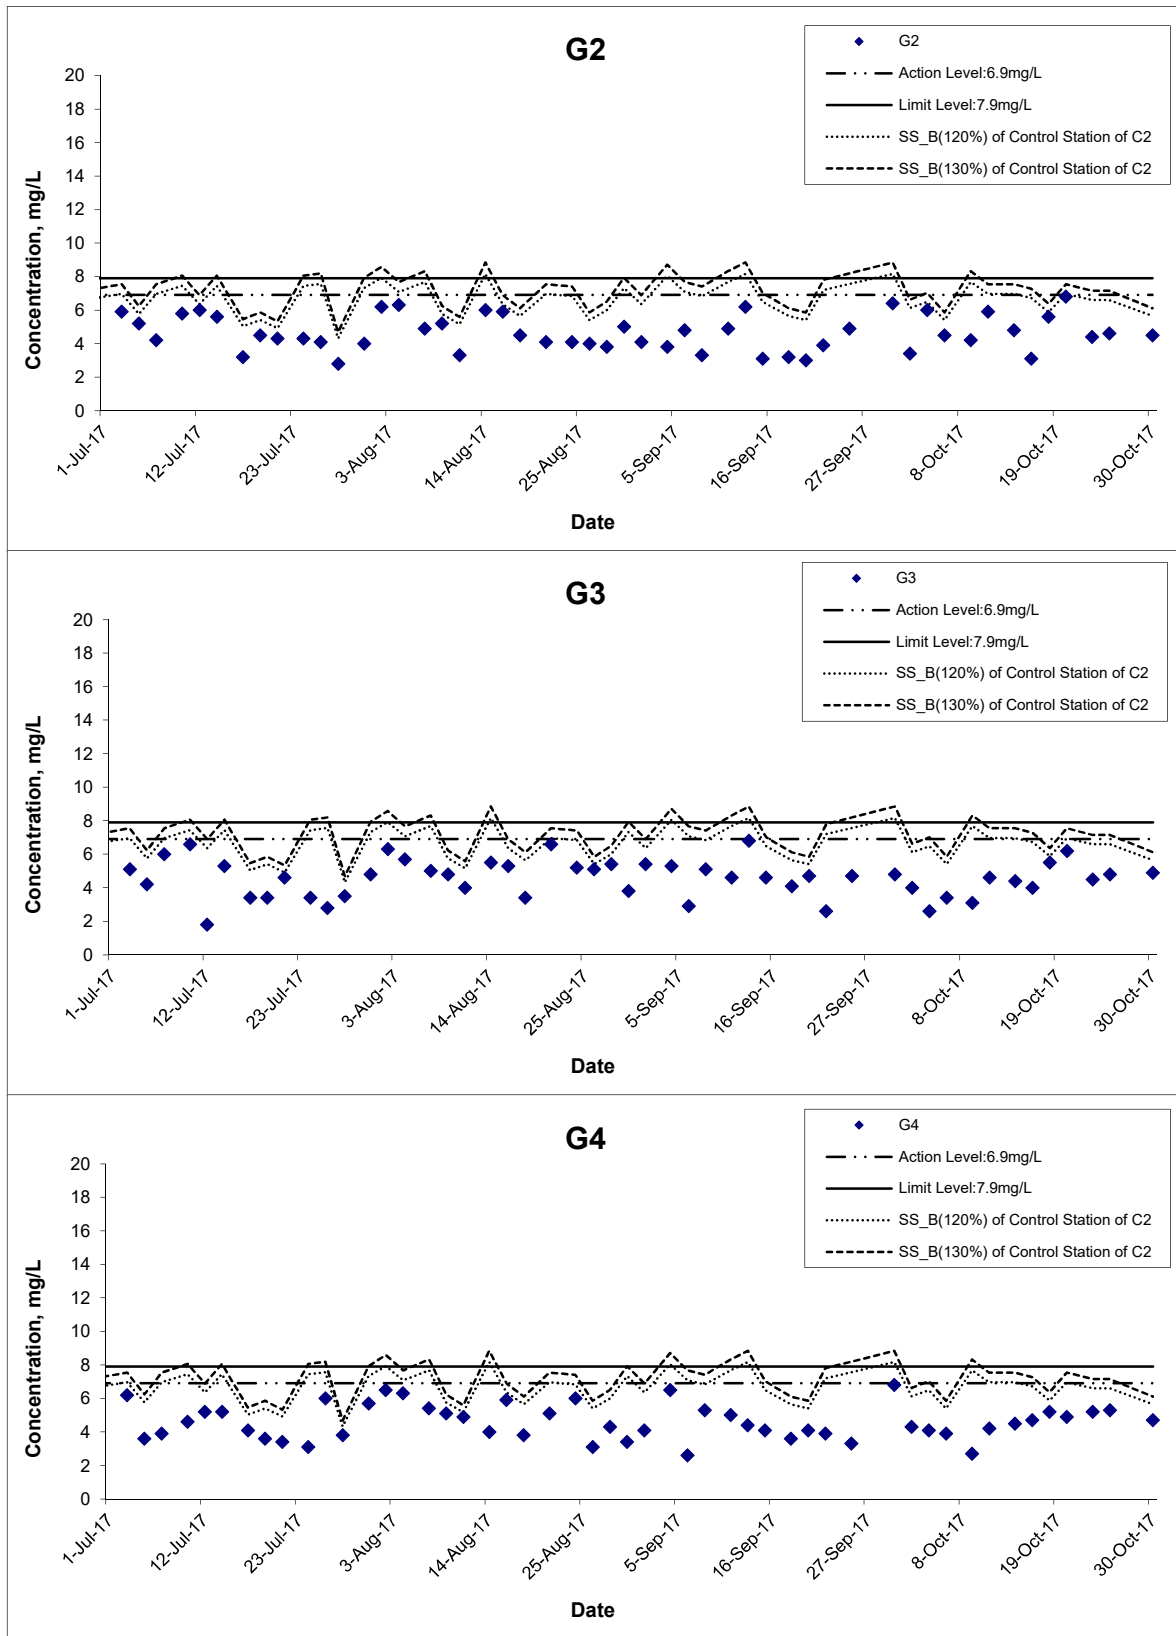

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Ebb Tide

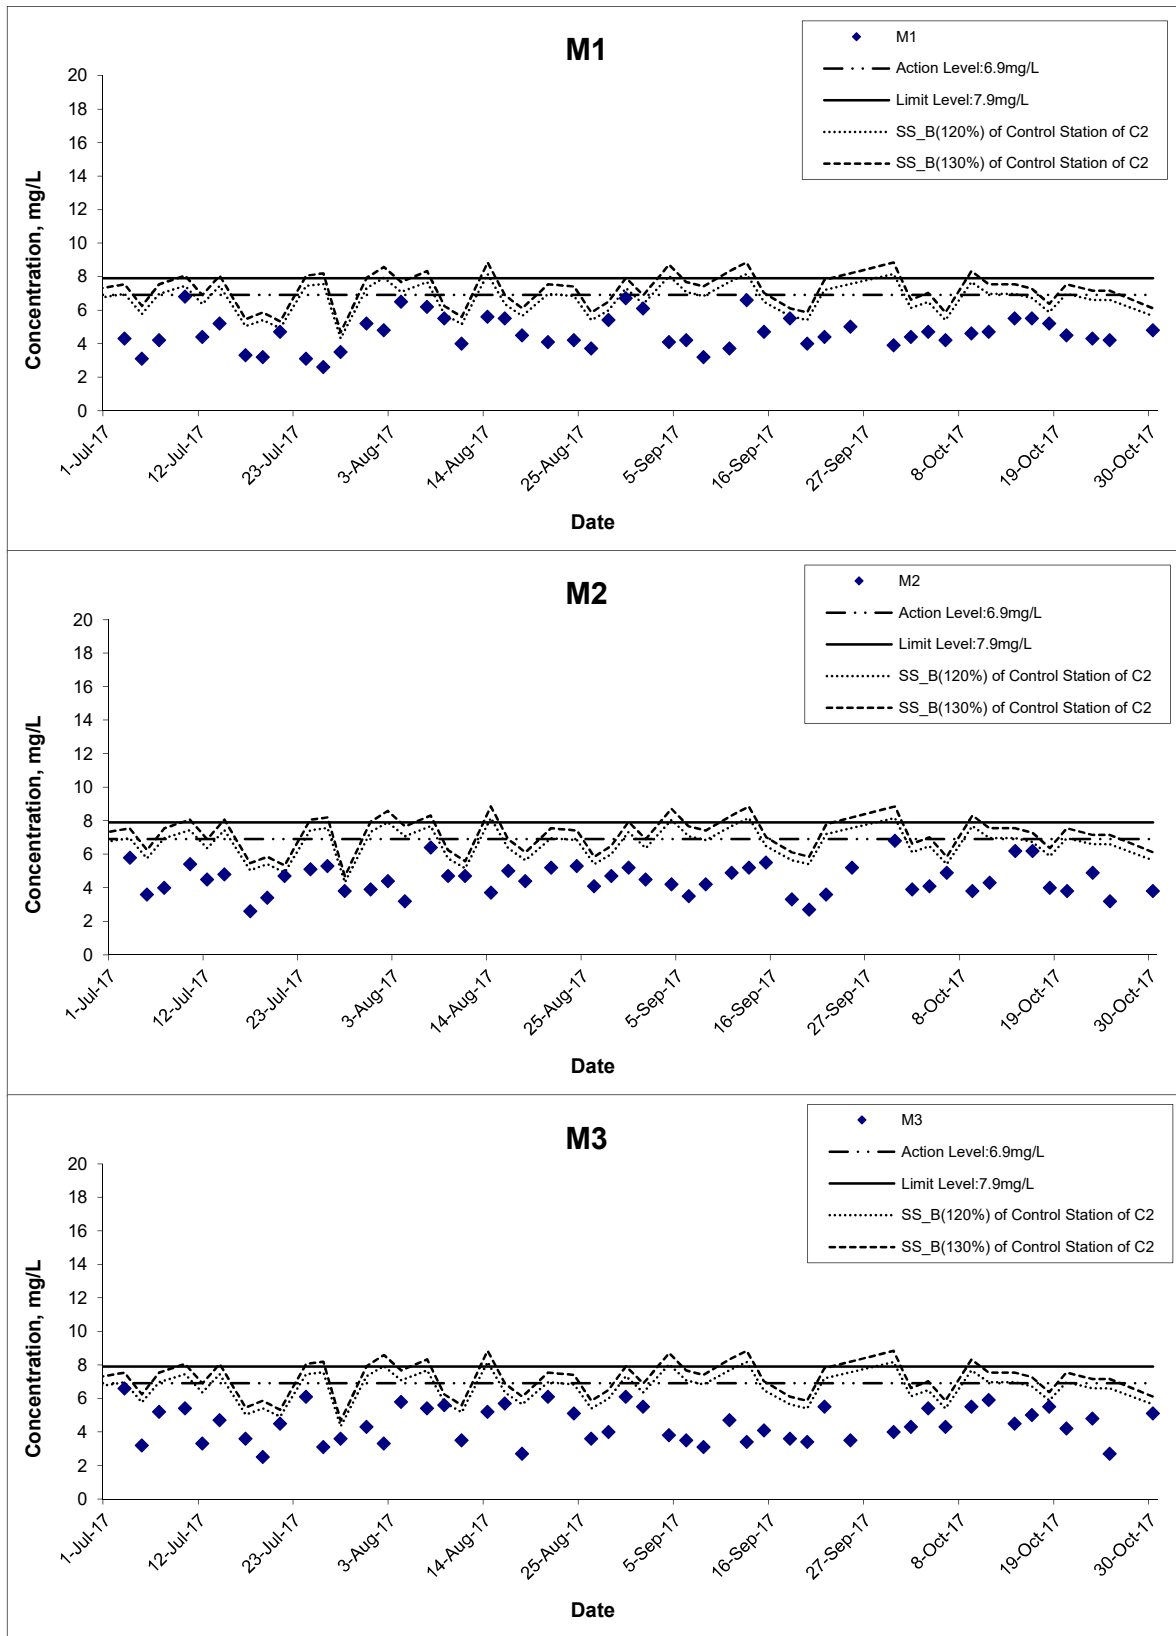

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Ebb Tide

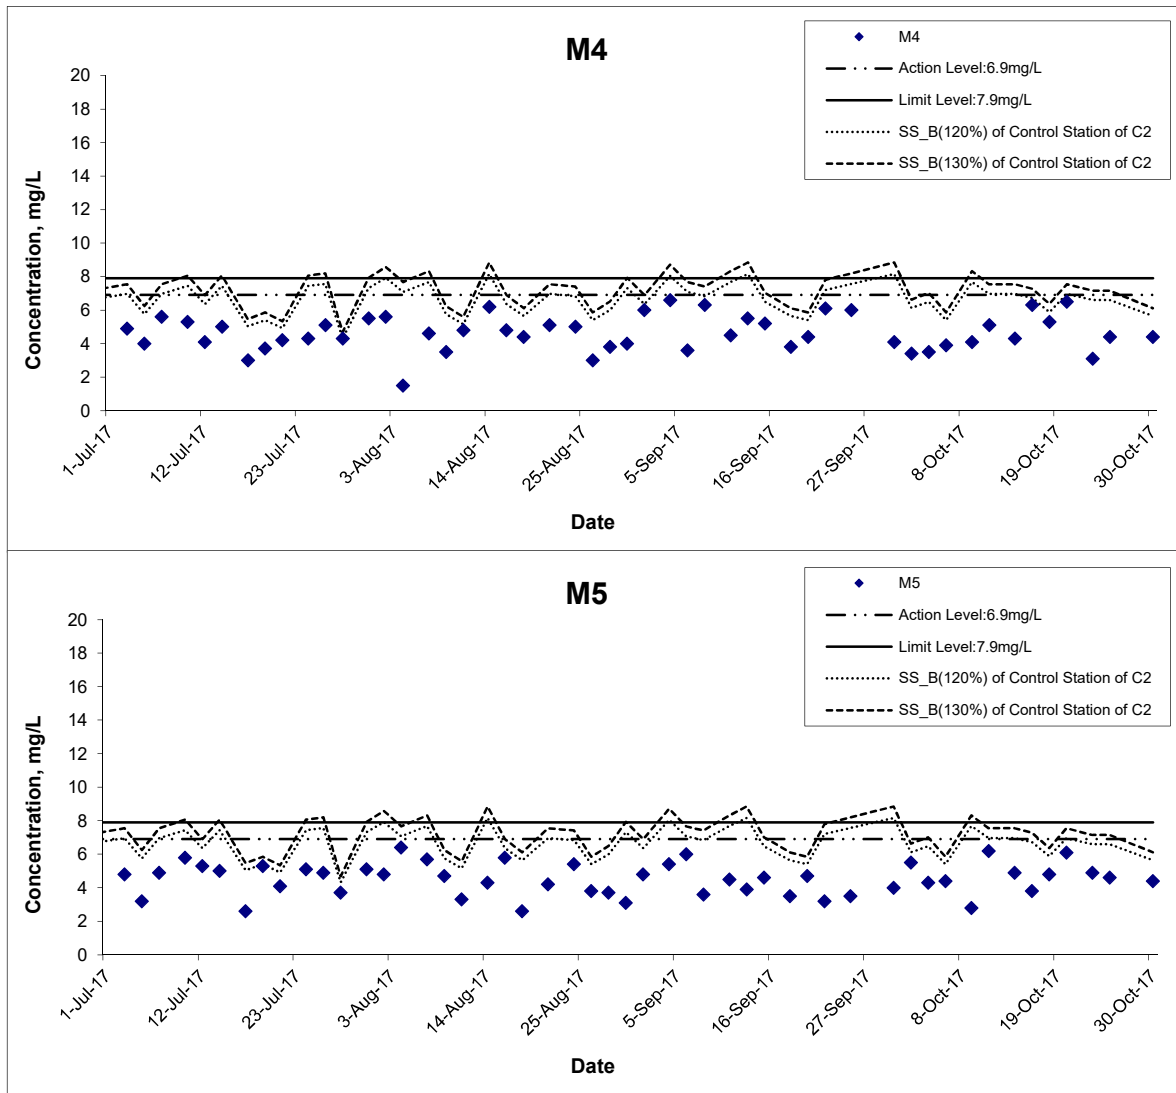

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S




Date Oct 17

Project No. MA16034

Appendix I






Suspended Solids (Bottom) at Mid-Flood Tide

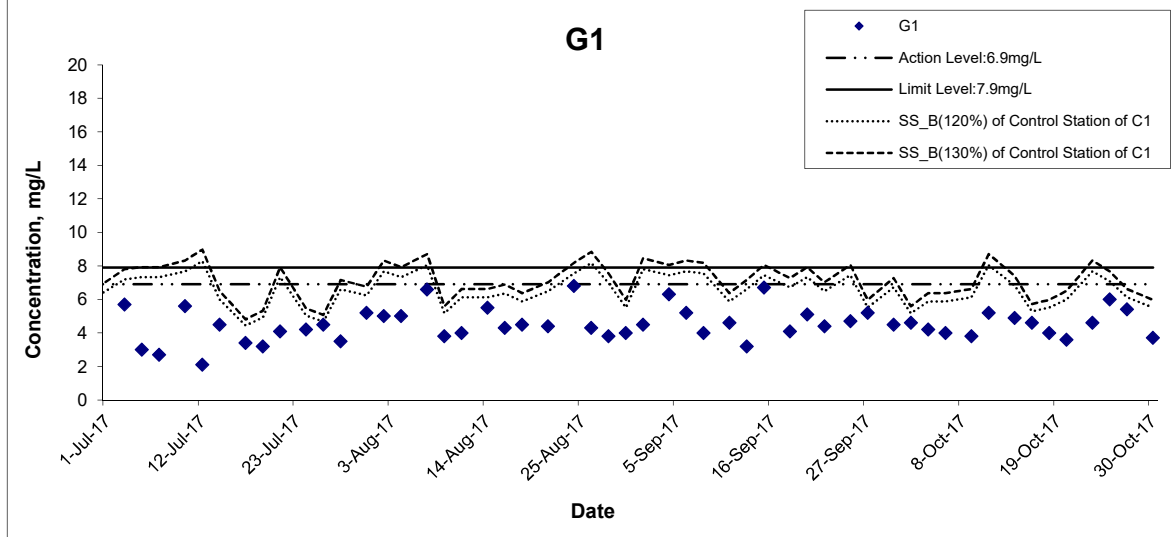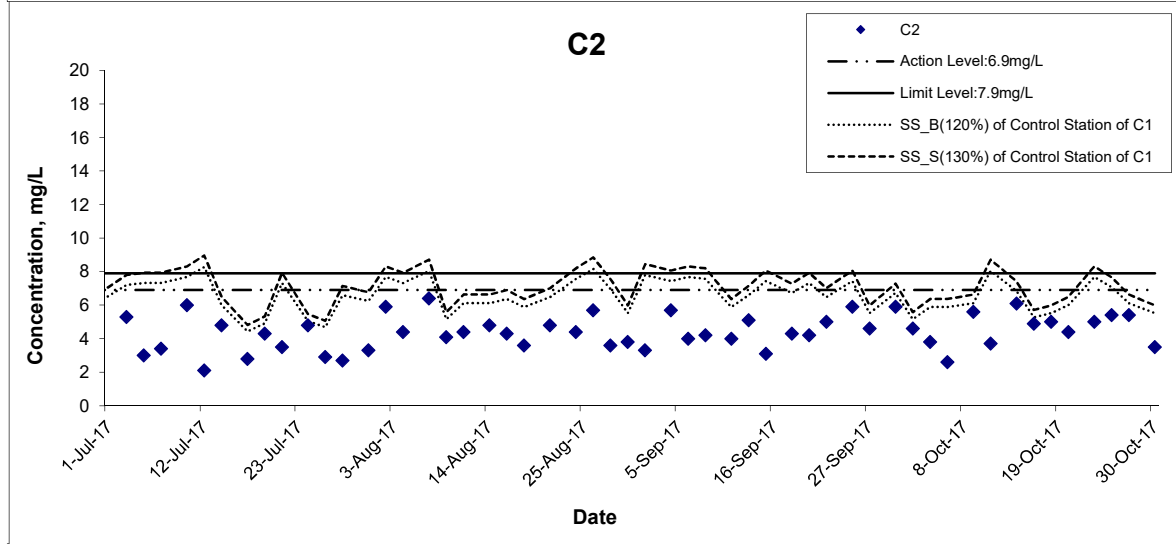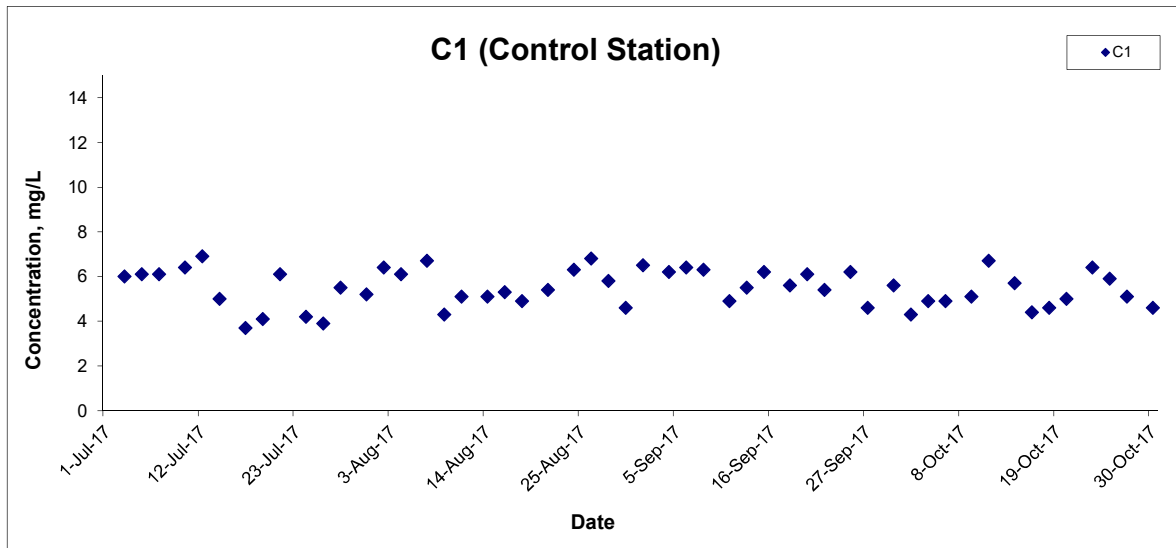

| | | | | | | |
|-------|--|-------|--------|-------------|---------|----------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Water Quality Monitoring Results | Date | Oct 17 | Appendix | I | |

Suspended Solids (Bottom) at Mid-Flood Tide

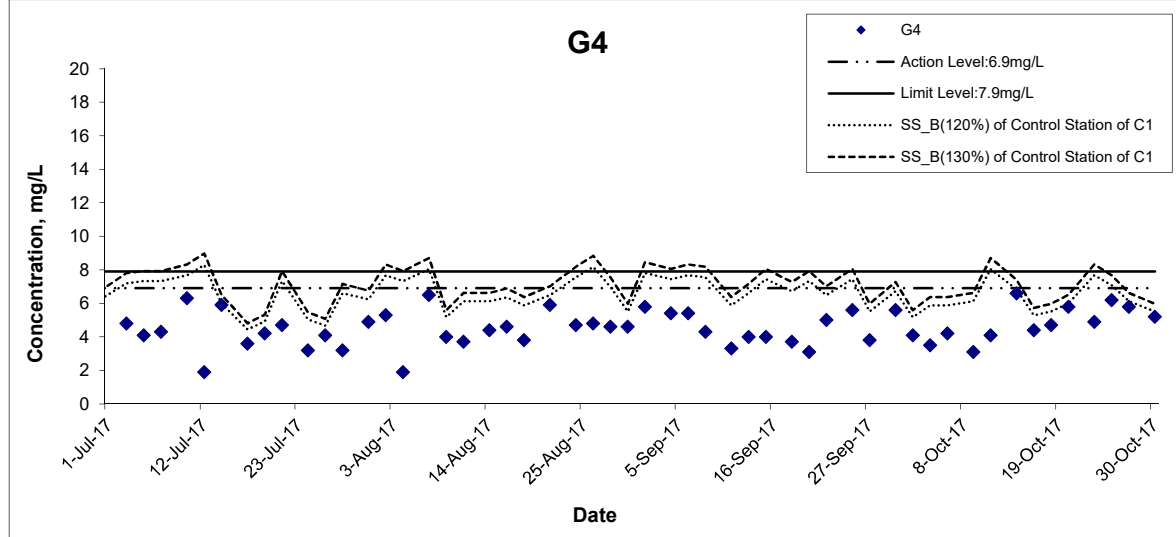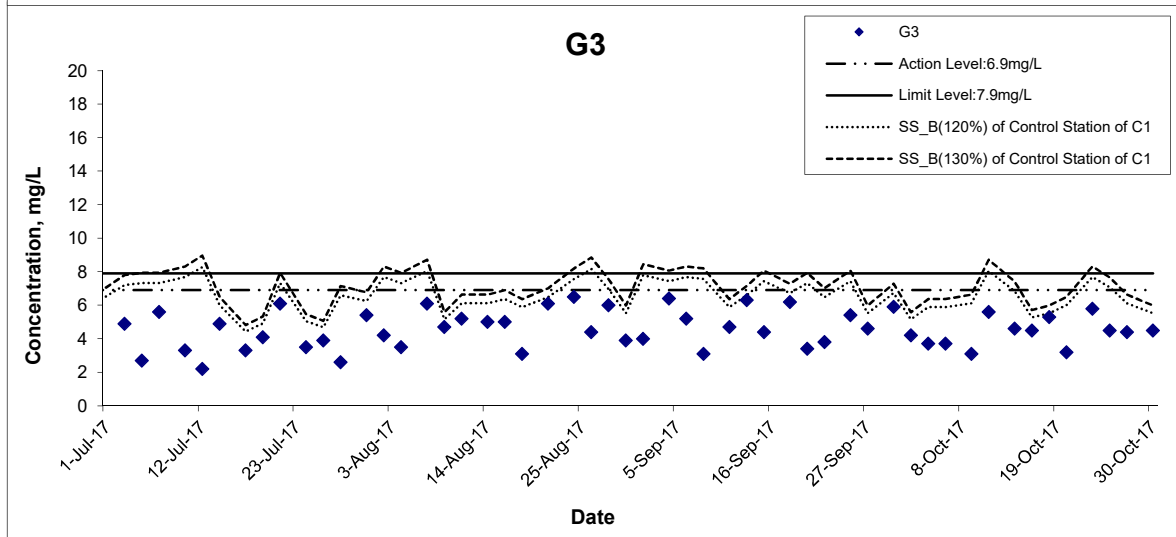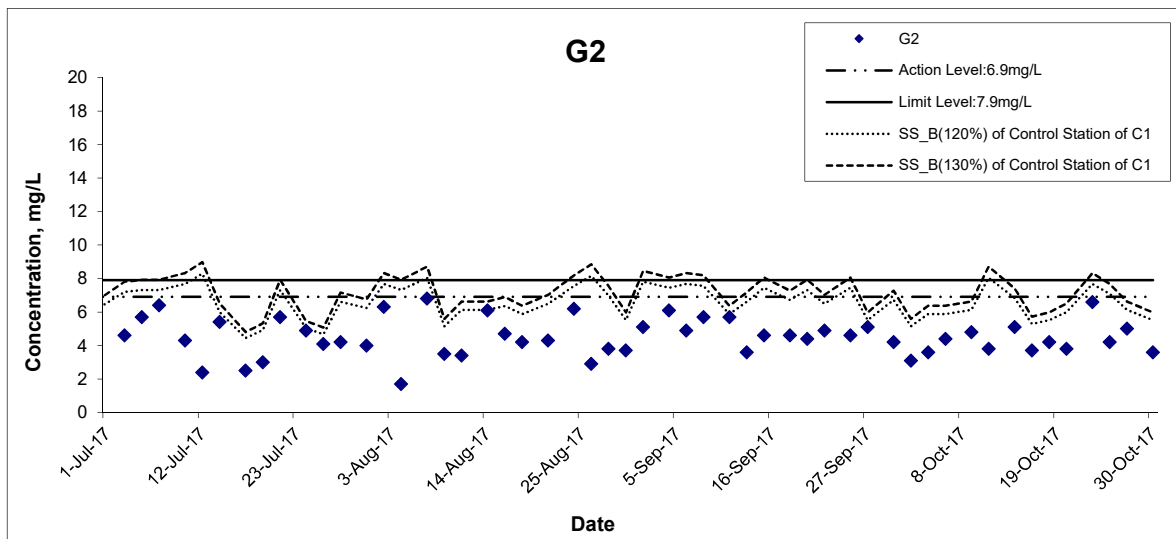

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S




Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Flood Tide

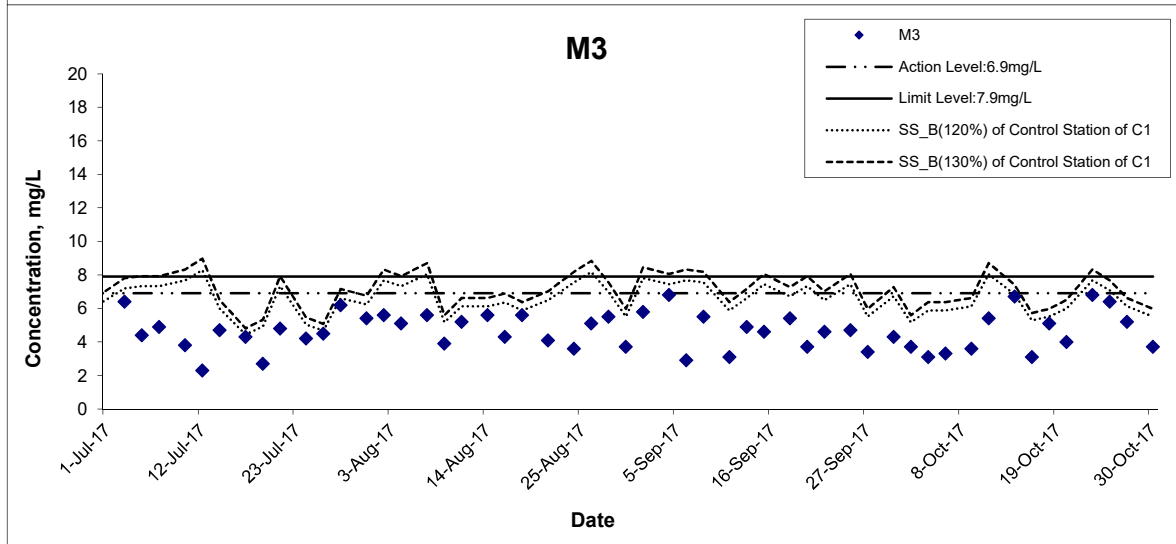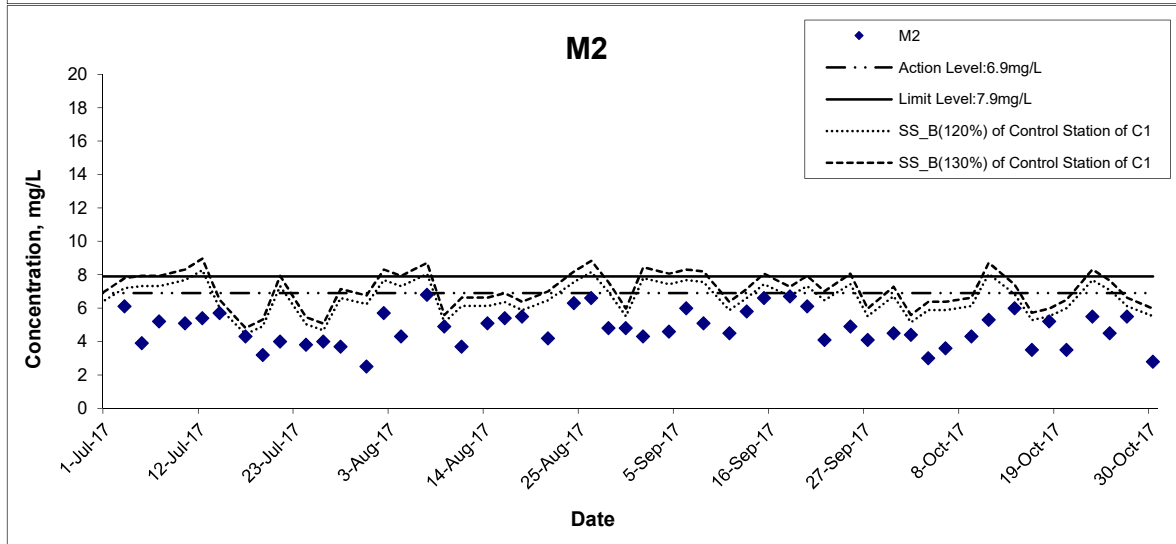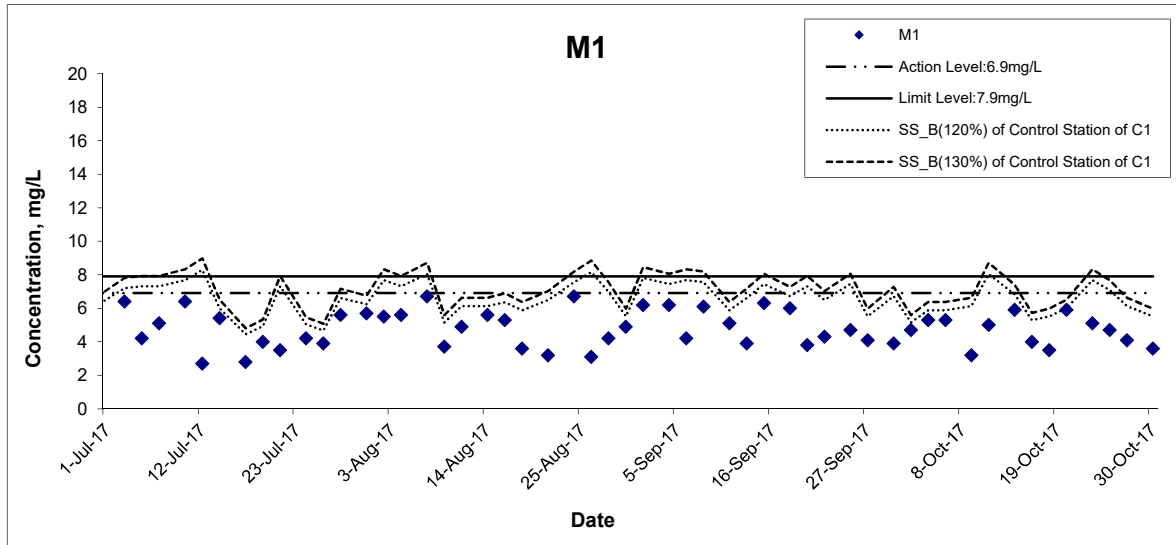

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Flood Tide

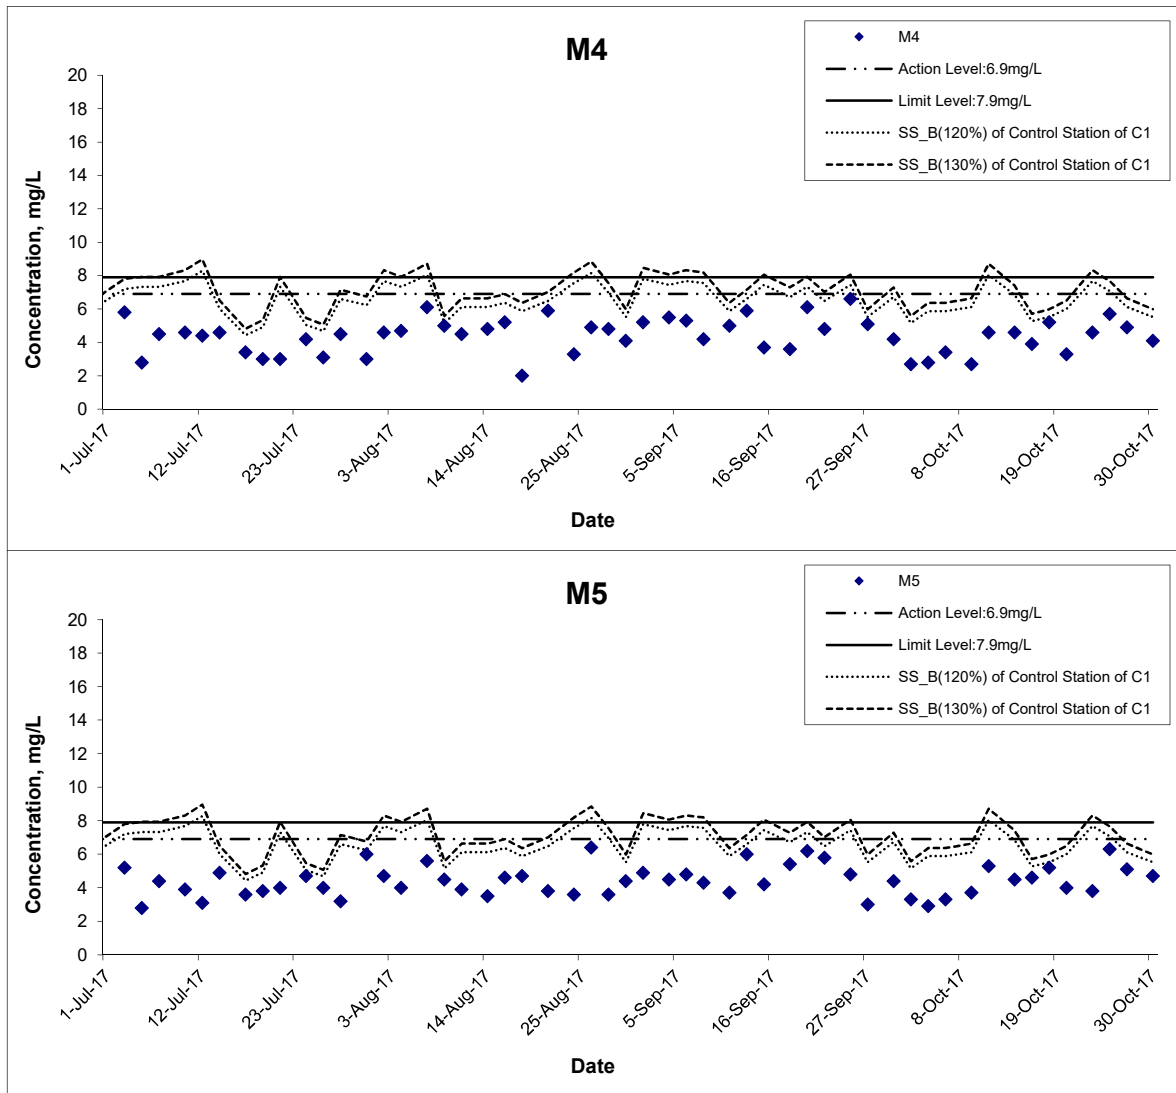

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Oct 17

Project No. MA16034

Appendix I




Suspended Solids (Intake Level of WSD Salt Water Intake) at Mid-Ebb Tide

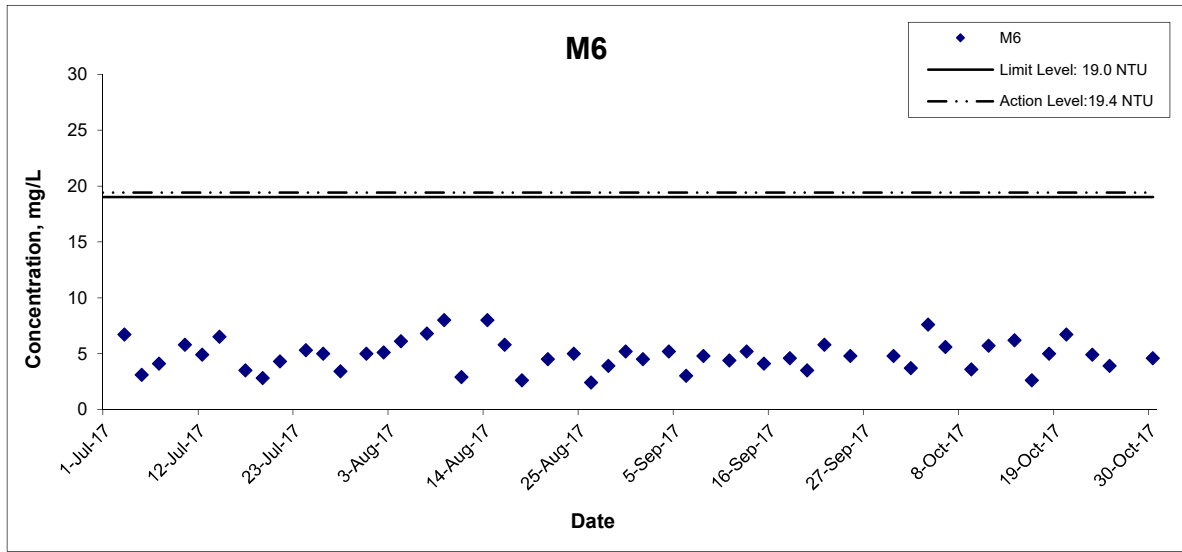

| | | | | | | |
|-------|--|-------|--------|-------------|---------|-----------------|
| Title | Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction | Scale | N.T.S | Project No. | MA16034 | CINOTECH |
| | Graphical Presentation of Water Quality Monitoring Results | Date | Oct 17 | Appendix | I | |

Suspended Solids (Intake Level of WSD Salt Water Intake) at Mid-Flood Tide

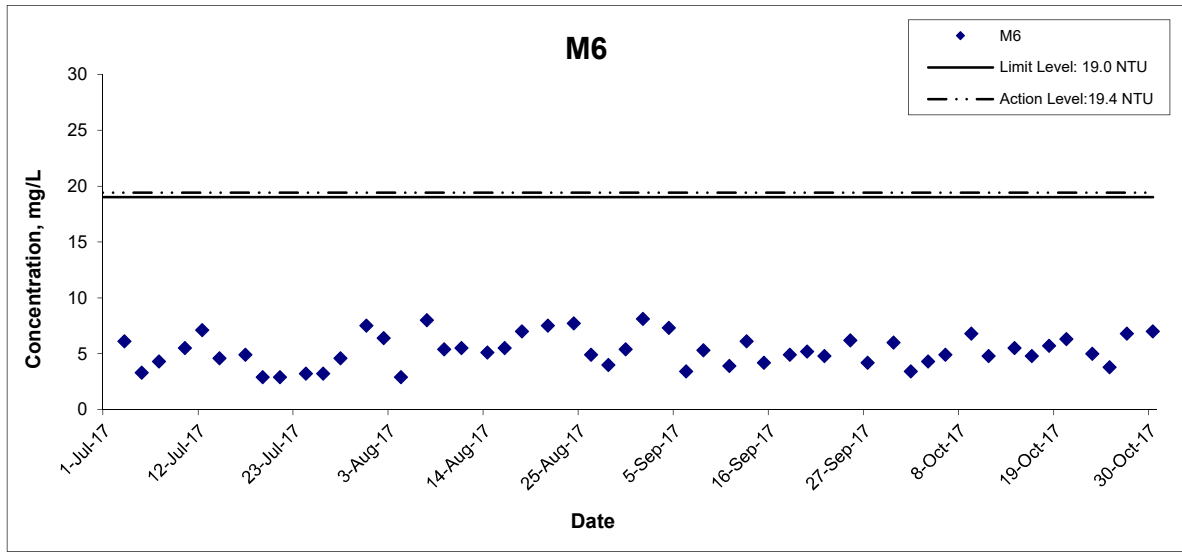

| | | | |
|---|----------------|------------------------|----------|
| Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Water Quality Monitoring Results | Scale N.T.S | Project No. MA16034 | CINOTECH |
| | Date Oct 17 | Appendix I | |

**APPENDIX J
QUALITY CONTROL REPORTS FOR
LABORATORY ANALYSIS**

TEST REPORT

APPLICANT: Cinotech Consultants Limited
1710, Technology Park,
18 On Lai Street,
Shatin, N.T.

| | |
|-----------------|------------|
| Report No.: | QC27657 |
| Date of Issue: | 2017-10-23 |
| Date Received: | 2017-10-12 |
| Date Tested: | 2017-10-12 |
| Date Completed: | 2017-10-23 |

ATTN: Ms. Mei Ling Tang
QC report:

Page: 1 of 2

Method Blank

| Parameter | MB 1 | Acceptance |
|---|-------|------------|
| Suspended Solids (SS) (mg/L) | <0.5 | <0.5 |
| Biochemical Oxygen Demand | N/A | N/A |
| Total Organic Carbon (mg-TOC/L) | <0.2 | <0.2 |
| Nitrogen (Total Kjeldahl + nitrate + nitrite) | N/A | N/A |
| Ammonia (mg NH ₃ -N/L) | <0.01 | <0.01 |
| Total Phosphorus (mg-P/L) | <0.01 | <0.01 |

Method QC

| Parameter | MQC1 | Acceptance |
|--|------|------------|
| Suspended Solids (SS) (%) | 99 | 80-120 |
| Biochemical Oxygen Demand (mg O ₂ /L) | 207 | 170-220 |
| Total Organic Carbon (%) | 96 | 80-120 |
| Nitrogen (Total Kjeldahl + nitrate + nitrite) | N/A | N/A |
| Ammonia (%) | 88 | 80-120 |
| Total Phosphorus (%) | 92 | 80-120 |

- Remarks: 1) < = less than
2) N/A = Not applicable
3) This report is the summary of quality control data for report number 27657.

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

| | |
|-----------------|------------|
| Report No.: | QC27657 |
| Date of Issue: | 2017-10-23 |
| Date Received: | 2017-10-12 |
| Date Tested: | 2017-10-12 |
| Date Completed: | 2017-10-23 |

Page: 2 of 2

QC report:

Sample Duplicate

| Parameter | 27657-3 chk | Acceptance |
|---|-------------|----------------|
| Suspended Solids (SS) (%) | 2 | RPD \leq 20% |
| Biochemical Oxygen Demand (%) | N/A | RPD \leq 20% |
| Total Organic Carbon (%) | 2 | RPD \leq 20% |
| Nitrogen (Total Kjeldahl + nitrate + nitrite) | N/A | N/A |
| Ammonia (%) | 1 | RPD \leq 20% |
| Total Phosphorus (%) | N/A | RPD \leq 20% |

Sample Spike

| Parameter | 27657-3 spk | Acceptance |
|---|-------------|------------|
| Suspended Solids (SS) (%) | N/A | N/A |
| Biochemical Oxygen Demand (%) | N/A | N/A |
| Total Organic Carbon (%) | 89 | 80-120 |
| Nitrogen (Total Kjeldahl + nitrate + nitrite) | N/A | N/A |
| Ammonia (%) | 90 | 80-120 |
| Total Phosphorus (%) | 94 | 80-120 |

Remarks: 1) \leq less than

2) N/A = Not applicable

3) This report is the summary of quality control data for report number 27657.

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
1710, Technology Park,
18 On Lai Street,
Shatin, N.T.

| | |
|-----------------|------------|
| Report No.: | QC27738 |
| Date of Issue: | 2017-11-08 |
| Date Received: | 2017-10-26 |
| Date Tested: | 2017-10-26 |
| Date Completed: | 2017-11-08 |

ATTN: Ms. Mei Ling Tang
QC report:

Page: 1 of 2

Method Blank

| Parameter | MB 1 | Acceptance |
|---|-------|------------|
| Suspended Solids (SS) (mg/L) | <0.5 | <0.5 |
| Biochemical Oxygen Demand | N/A | N/A |
| Total Organic Carbon (mg-TOC/L) | <0.2 | <0.2 |
| Nitrogen (Total Kjeldahl + nitrate + nitrite) | N/A | N/A |
| Ammonia (mg NH ₃ -N/L) | <0.01 | <0.01 |
| Total Phosphorus (mg-P/L) | <0.01 | <0.01 |

Method QC

| Parameter | MQC1 | Acceptance |
|--|------|------------|
| Suspended Solids (SS) (%) | 99 | 80-120 |
| Biochemical Oxygen Demand (mg O ₂ /L) | 188 | 170-220 |
| Total Organic Carbon (%) | 107 | 80-120 |
| Nitrogen (Total Kjeldahl + nitrate + nitrite) | N/A | N/A |
| Ammonia (%) | 106 | 80-120 |
| Total Phosphorus (%) | 87 | 80-120 |

Remarks: 1) < = less than

2) N/A = Not applicable

3) This report is the summary of quality control data for report number 27738.

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

| | |
|-----------------|------------|
| Report No.: | QC27738 |
| Date of Issue: | 2017-11-08 |
| Date Received: | 2017-10-26 |
| Date Tested: | 2017-10-26 |
| Date Completed: | 2017-11-08 |

Page: 2 of 2

QC report:

Sample Duplicate

| Parameter | 27738-3 chk | Acceptance |
|---|-------------|----------------|
| Suspended Solids (SS) (%) | N/A | RPD \leq 20% |
| Biochemical Oxygen Demand (%) | N/A | RPD \leq 20% |
| Total Organic Carbon (%) | 1 | RPD \leq 20% |
| Nitrogen (Total Kjeldahl + nitrate + nitrite) | N/A | N/A |
| Ammonia (%) | N/A | RPD \leq 20% |
| Total Phosphorus (%) | N/A | RPD \leq 20% |

Sample Spike

| Parameter | 27738-3 spk | Acceptance |
|---|-------------|------------|
| Suspended Solids (SS) (%) | N/A | N/A |
| Biochemical Oxygen Demand (%) | N/A | N/A |
| Total Organic Carbon (%) | 103 | 80-120 |
| Nitrogen (Total Kjeldahl + nitrate + nitrite) | N/A | N/A |
| Ammonia (%) | 100 | 80-120 |
| Total Phosphorus (%) | 86 | 80-120 |

Remarks: 1) \leq less than

2) N/A = Not applicable

3) This report is the summary of quality control data for report number 27738.

*****END OF REPORT*****

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27605 |
| Date of Issue: | 2017/10/03 |
| Date Received: | 2017/10/02 |
| Date Tested: | 2017/10/02 |
| Date Completed: | 2017/10/03 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2017/10/02

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/171002

| Total Suspended Solids | Duplicate Analysis | | | QC Recovery, % |
|------------------------|--------------------|------------------|------------------|----------------|
| Sampling Point | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 5.2 | 5.2 | 0 | 99 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of WELLAB Ltd.



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27616 |
| Date of Issue: | 2017/10/06 |
| Date Received: | 2017/10/04 |
| Date Tested: | 2017/10/04 |
| Date Completed: | 2017/10/06 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2017/10/04

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/171004

| Total Suspended Solids Sampling Point | Duplicate Analysis | | | QC Recovery, % |
|--|--------------------|------------------|------------------|----------------|
| | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 5.6 | 5.5 | 1 | 103 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of WELLAB Ltd.



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27623 |
| Date of Issue: | 2017/10/09 |
| Date Received: | 2017/10/06 |
| Date Tested: | 2017/10/06 |
| Date Completed: | 2017/10/09 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2017/10/06

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/171006

| Total Suspended Solids | Duplicate Analysis | | | QC Recovery, % |
|------------------------|--------------------|------------------|------------------|----------------|
| Sampling Point | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 4.1 | 4.3 | 4 | 101 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27633 |
| Date of Issue: | 10/10/2017 |
| Date Received: | 9/10/2017 |
| Date Tested: | 9/10/2017 |
| Date Completed: | 10/10/2017 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 9/10/2017

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/171010

| Total Suspended Solids | Duplicate Analysis | | | QC Recovery, % |
|------------------------|--------------------|------------------|------------------|----------------|
| Sampling Point | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 4.0 | 4.2 | 3 | 101 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27643 |
| Date of Issue: | 12/10/2017 |
| Date Received: | 11/10/2017 |
| Date Tested: | 11/10/2017 |
| Date Completed: | 12/10/2017 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 11/10/2017

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/171011

| Total Suspended Solids | Duplicate Analysis | | | QC Recovery, % |
|------------------------|--------------------|------------------|------------------|----------------|
| Sampling Point | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 3.6 | 3.7 | 2 | 103 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27662 |
| Date of Issue: | 16/10/2017 |
| Date Received: | 14/10/2017 |
| Date Tested: | 14/10/2017 |
| Date Completed: | 16/10/2017 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 14/10/2017

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/171014

| Total Suspended Solids | Duplicate Analysis | | | QC Recovery, % |
|------------------------|--------------------|------------------|------------------|----------------|
| Sampling Point | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 5.0 | 4.8 | 3 | 100 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27666 |
| Date of Issue: | 17/10/2017 |
| Date Received: | 16/10/2017 |
| Date Tested: | 16/10/2017 |
| Date Completed: | 17/10/2017 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)
Project No.: MA16034
Sampling Date: 16/10/2017
Number of Sample: 136
Custody No.: MA16034-CE/59/2015(EP)/171016

| Total Suspended Solids | Duplicate Analysis | | | QC Recovery, % |
|------------------------|--------------------|------------------|------------------|----------------|
| Sampling Point | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 5.3 | 5.5 | 2 | 96 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27679 |
| Date of Issue: | 19/10/2017 |
| Date Received: | 18/10/2017 |
| Date Tested: | 18/10/2017 |
| Date Completed: | 19/10/2017 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)
Project No.: MA16034
Sampling Date: 18/10/2017
Number of Sample: 136
Custody No.: MA16034-CE/59/2015(EP)/171018

| Total Suspended Solids | Duplicate Analysis | | | QC Recovery, % |
|------------------------|--------------------|------------------|------------------|----------------|
| Sampling Point | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 4.7 | 4.3 | 9 | 101 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of WELLAB Ltd.



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27695 |
| Date of Issue: | 23/10/2017 |
| Date Received: | 20/10/2017 |
| Date Tested: | 20/10/2017 |
| Date Completed: | 23/10/2017 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 20/10/2017

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/171020

| Total Suspended Solids Sampling Point | Duplicate Analysis | | | QC Recovery, % |
|--|--------------------|------------------|------------------|----------------|
| | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 5.5 | 5.6 | 3 | 100 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of WELLAB Ltd.



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27701 |
| Date of Issue: | 24/10/2017 |
| Date Received: | 23/10/2017 |
| Date Tested: | 23/10/2017 |
| Date Completed: | 24/10/2017 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)
Project No.: MA16034
Sampling Date: 23/10/2017
Number of Sample: 136
Custody No.: MA16034-CE/59/2015(EP)/171023

| Total Suspended Solids Sampling Point | Duplicate Analysis | | | QC Recovery, % |
|--|--------------------|------------------|------------------|----------------|
| | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 4.5 | 4.9 | 7 | 100 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27719 |
| Date of Issue: | 26/10/2017 |
| Date Received: | 25/10/2017 |
| Date Tested: | 25/10/2017 |
| Date Completed: | 26/10/2017 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 25/10/2017

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/171025

| Total Suspended Solids | Duplicate Analysis | | | QC Recovery, % |
|------------------------|--------------------|------------------|------------------|----------------|
| Sampling Point | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 4.1 | 3.9 | 4 | 99 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27735 |
| Date of Issue: | 30/10/2017 |
| Date Received: | 27/10/2017 |
| Date Tested: | 27/10/2017 |
| Date Completed: | 30/10/2017 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 27/10/2017

Number of Sample: 68

Custody No.: MA16034-CE/59/2015(EP)/171027

| Total Suspended Solids | Duplicate Analysis | | | QC Recovery, % |
|------------------------|--------------------|------------------|------------------|----------------|
| Sampling Point | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4sf | 3.2 | 3.1 | 3 | 98 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

| | |
|-----------------|------------|
| Report No.: | 27745 |
| Date of Issue: | 31/10/2017 |
| Date Received: | 30/10/2017 |
| Date Tested: | 30/10/2017 |
| Date Completed: | 31/10/2017 |

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 30/10/2017

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/171030

| Total Suspended Solids Sampling Point | Duplicate Analysis | | | QC Recovery, % |
|--|--------------------|------------------|------------------|----------------|
| | Trial 1, mg/L | Trial 2, mg/L | Difference, % | |
| M4se | 5.6 | 5.7 | 1 | 103 |

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

**APPENDIX K
SUMMARY OF EXCEEDANCE**

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel –
Design and Construction

Appendix K – Summary of Exceedance

Reporting Period: October 2017

(A) Exceedance Report for Air Quality
(NIL in the reporting month)

(B) Exceedance Report for Construction Noise

Action Level for Construction Noise

(Five Action Level exceedance was recorded due to the documented complaints received in this reporting month.)

Limit Level for Construction Noise

(One Limit Level exceedance was recorded on 12 October 2017 at CM1)

| Station | Location | Time | Measured Level (Leq dB(A)) | Baseline Noise Level (Leq dB(A)) | Construction Noise Level (Leq dB(A)) | Action Level | Limit Level (Leq dB(A)) | Level exceeded |
|---------|---|----------------------|----------------------------|----------------------------------|--------------------------------------|---|-------------------------|----------------|
| CM1 | Nga Lai House, Yau Lai Estate Phase 1, Yau Tong | 10:30 | 76.2 | 65.5 | <u>75.8</u> | When one documented complaint is received | 75.0 | Limit |
| | | 11:00 ⁽¹⁾ | 75.6 | 65.5 | <u>75.2</u> | When one documented complaint is received | 75.0 | Limit |

(1) Repeated measurement according to Event and Action Plan for Construction Noise of the EM&A Manual

According to the Event and Action Plan for Construction Noise in the EM&A Manual, ET has increased noise monitoring frequency to check the effectiveness of Contractor's remedial action to twice a week in October 2017. No Limit Level Exceedance are recorded.

(C) Exceedance Report for Water Quality

(One Action Level exceedance in groundwater quality monitoring as followed:

| Date | Monitoring Location | Monitoring Parameter | Monitoring Results | Action Level | Limit Level |
|-------------|---------------------|----------------------|--------------------|--------------|-------------|
| 12 Oct 2017 | Stream 2 | Suspended Solids | 10 mg/L | 7.6 | 12.1 |

It is considered that the exceedance is not project-related as there was no tunnel boring or tunnel construction works in Tseung Kwan O side in this reporting period.

(No exceedance for marine water quality monitoring in the reporting month)

(D) Exceedance Report for Ecology
(NIL in the reporting month)

(E) Exceedance Report for Cultural Heritage
(NIL in the reporting month)

(F) Exceedance Report for Landfill Gas
(NIL in the reporting month)

**APPENDIX L
SITE AUDIT SUMMARY**

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction
Monthly EM&A Report

Appendix L - Site Audit Summary (October 2017)

Contract No. NE/2015/01

Tseung Kwan O - Lam Tin Tunnel - Main Tunnel and Associated Works

| Items | Date | Status* | Follow up Action |
|---|-------------------|----------------|---|
| <i>Water Quality</i> | | | |
| The Contractor was reminded to treat site runoff at TKO site with wastewater treatment facility below the BMCPC pathway before discharge. | 20 September 2017 | ✗ | Item remarked on 27 September 2017. |
| | 27 September 2017 | ✗ | Item remarked on 04 October 2017. |
| | 04 October 2017. | ✓ | Improved/rectified on 11 October 2017. |
| The Contractor was reminded to extend the geotextile of silt curtain to the seabed at TKO site to prevent silty discharge. | 04 October 2017 | ✓ | Improved/rectified on 11 October 2017. |
| <i>Noise</i> | | | |
| Noise barriers at Portion IVC should be erected to reduce noise nuisance to nearby NSRs. | 13 September 2017 | ✗ | Item remarked on 20 September 2017. |
| | 20 September 2017 | ✗ | Item remarked on 27 September 2017. |
| | 27 September 2017 | ✗ | Item remarked on 04 October 2017. |
| | 04 October 2017 | ✗ | Item remarked on 11 October 2017. |
| | 11 October 2017 | ✗ | Item remarked on 18 October 2017. |
| | 18 October 2017 | ✓ | Improved/rectified on 25 October 2017. |
| <i>Landscape and Visual</i> | | | |
| -- | -- | -- | -- |
| <i>Air Quality</i> | | | |
| Water spraying should be provided to breaking works at Slope F at Lam Tin Interchange for dust suppression. | 27 September 2017 | ✓ | Improved/rectified on 04 October 2017. |
| Dust screens should be erected at Portion 6 at TKO (near BMCPC pathway) to reduce fugitive emission. | 11 October 2017 | ✓ | Improved/rectified on 18 October 2017. |
| Dark smoke emitted from generator near Portion 2a at LTI should be avoided. | 18 October 2017 | ✓ | Improved/rectified on 25 October 2017. |
| Water spraying should be provided more frequently at the haul road of LTI for dust suppression. | 18 October 2017 | ✓ | Improved/rectified on 25 October 2017. |
| Water spraying should be provided more frequently to open slopes at LTI for dust suppression. | 25 October 2017 | # | Follow up action will be reported in next reporting month |
| <i>Waste / Chemical Management</i> | | | |
| Oil stains at Portion IVC (near site entrance) should be properly disposed of as chemical waste. | 27 September 2017 | ✗ | Item remarked on 04 October 2017. |
| | 04 October 2017 | ✓ | Improved/rectified on 11 October 2017. |
| Drip tray should be provided to chemical containers at Portion IVC (near site entrance). | 11 October 2017 | ✓ | Improved/rectified on 18 October 2017. |
| Drip tray should be provided to air compressors near the scaffolds at Portion 6 at TKO site. | 25 October 2017 | # | Follow up action will be reported in next reporting month |
| <i>Impact on Cultural Heritage</i> | | | |
| -- | -- | -- | -- |
| <i>Permits / Licenses</i> | | | |
| -- | -- | -- | -- |

Appendix L - Site Audit Summary (October 2017)

- ✓ Observation/reminder was made during site audit but improved/rectified by the contractor in the next site audit
- ✗ Observation/reminder was made during site audit but not yet improved/rectified by the contractor in the next site audit
- # Follow up action will be reported in next reporting month
- * Non-compliance of mitigation measure
- Non-compliance but improved by the contractor

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction
Monthly EM&A Report

Appendix L - Site Audit Summary (October 2017)

Contract No. NE/2015/02

Tseung Kwan O - Lam Tin Tunnel - Road P2 and Associated Works

| Items | Date | Status* | Follow up Action |
|--|-------------------|----------------|---|
| <i>Water Quality</i> | | | |
| The Contractor was reminded to provide bunds to the gaps found at the edge of double water gate's deck so as to prevent the escape of materials into the surrounding waters. | 26 October 2017 | # | Follow up action will be reported in next reporting month |
| The Contractor was reminded to clear the accumulated silt & sediment in the ditch near the site entrance of Tong Yin Street regularly. | 26 October 2017 | # | Follow up action will be reported in next reporting month |
| Stockpiles of dusty material were observed in the steel tanks (the west of Type 2 cofferdam). The Contractor should provide preventive measures to avoid overflow of dusty material. | 26 October 2017 | # | Follow up action will be reported in next reporting month |
| <i>Noise</i> | | | |
| The Contractor was reminded to erect noise barrier properly before commencement of work in Portion 4 to reduce noise nuisance. | 17 October 2017 | ✓ | Improved/rectified on 26 October 2017. |
| <i>Landscape and Visual</i> | | | |
| -- | -- | -- | -- |
| <i>Air Quality</i> | | | |
| The Contractor was reminded to cover the open stockpiles of dusty materials in Work Area A. | 27 September 2017 | ✓ | Improved/rectified on 06 October 2017. |
| <i>Waste / Chemical Management</i> | | | |
| Stagnant water was observed in drip trays at Portion 8 near the worker's rest area, the Contractor was reminded to clear stagnant water regularly. | 06 October 2017 | ✓ | Improved/rectified on 12 October 2017. |
| <i>Impact on Cultural Heritage</i> | | | |
| -- | -- | -- | -- |
| <i>Permits / Licenses</i> | | | |
| -- | -- | -- | -- |

- ✓ Observation/reminder was made during site audit but improved/rectified by the contractor in the next site audit
- ✗ Observation/reminder was made during site audit but not yet improved/rectified by the contractor in the next site audit
- # Follow up action will be reported in next reporting month

- * Non-compliance of mitigation measure
- Non-compliance but rectified by the contractor

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction
Monthly EM&A Report

Appendix L - Site Audit Summary (October 2017)

Contract No. NE/2015/03

Tseung Kwan O - Lam Tin Tunnel - Northern Footbridge

| Items | Date | Status* | Follow up Action |
|---|-----------------|---------|--|
| Water Quality | | | |
| -- | -- | -- | -- |
| Noise | | | |
| -- | -- | -- | -- |
| Landscape and Visual | | | |
| -- | -- | -- | -- |
| Air Quality | | | |
| -- | -- | -- | -- |
| Waste / Chemical Management | | | |
| Water is accumulated in the drip tray of the generator at East Pier. The Contractor is reminded to clean up regularly and properly. | 09 October 2017 | ✓ | Improved/rectified on 19 October 2017. |
| Impact on Cultural Heritage | | | |
| -- | -- | -- | -- |
| Permits / Licenses | | | |
| -- | -- | -- | -- |

- ✓ Observation/reminder was made during site audit but improved/rectified by the contractor in the next site audit
- ✗ Observation/reminder was made during site audit but not yet improved/rectified by the contractor in the next site audit
- # Follow up action will be reported in next reporting month
- * Non-compliance of mitigation measure
- Non-compliance but rectified by the contractor

**APPENDIX M
EVENT AND ACTION PLANS**

Event and Action Plan for Air Quality (Dust)

| EVENT | ACTION | | | |
|---|---|---|--|---|
| | ET | IEC | ER | CONTRACTOR |
| Action level being exceeded by one sampling | <ol style="list-style-type: none"> 1. Identify source, investigate the causes of complaint and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. | <ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. | <ol style="list-style-type: none"> 1. Notify Contractor. | <ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate. |
| Action level being exceeded by two or more consecutive sampling | <ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; | <ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. | <ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. | <ol style="list-style-type: none"> 1. Submit proposals for remedial actions to IEC within three working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate. |

| EVENT | ACTION | | | |
|--|---|---|--|--|
| | ET | IEC | ER | CONTRACTOR |
| | 8. If exceedance stops, cease additional monitoring. | | | |
| Limit level being exceeded by one sampling | <ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform Contractor, IEC, ER, and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. | <ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. | <ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. | <ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within three working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate. |
| Limit level being exceeded by two or more consecutive sampling | <ol style="list-style-type: none"> 1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; | <ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; | <ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; | <ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within three working days of notification; 3. Implement the agreed proposals; |

| EVENT | ACTION | | | |
|-------|---|---|--|--|
| | ET | IEC | ER | CONTRACTOR |
| | 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. | 3. Supervise the implementation of remedial measures. | 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. | 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated. |

Event and Action Plan for Construction Noise

| EVENT | ACTION | | | |
|--------------|--|---|--|---|
| | ET | IEC | ER | CONTRACTOR |
| Action Level | <ol style="list-style-type: none"> 1. Notify IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness. | <ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Supervise the implementation of remedial measures. | <ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented. | <ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC; 2. Implement noise mitigation proposals. |
| Limit Level | <ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC, ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances; | <ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. | <ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. | <ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated. |

| EVENT | ACTION | | | |
|-------|--|-----|----|------------|
| | ET | IEC | ER | CONTRACTOR |
| | 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. | | | |

Event and Action Plan for Marine Water Quality

| Event | Action | | | |
|--|---|---|---|---|
| | ET | IEC | ER | CONTRACTOR |
| Action level being exceeded by one sampling day at water sensitive receiver(s) | <ul style="list-style-type: none"> Identify the source(s) of impact by comparing the results with those collected at the control stations as appropriate; If exceedance is found to be caused by the reclamation activities, repeat <i>in-situ</i> measurement to confirm findings; Inform IEC and contractor; Check monitoring data, all plant, equipment and Contractor's working methods; If exceedance occurs at WSD salt water intake, inform WSD; Discuss mitigation measures with IEC and Contractor; Repeat measurement on next day of exceedance. | <ul style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; Review proposal on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. | <ul style="list-style-type: none"> Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation proposal. | <ul style="list-style-type: none"> Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Amend working methods if appropriate; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agree mitigation measures. |
| Action level being exceeded by two or more consecutive | <ul style="list-style-type: none"> Identify the source(s) of impact by comparing the results with those collected at the control stations as appropriate; | <ul style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; | <ul style="list-style-type: none"> Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation proposal; | <ul style="list-style-type: none"> Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; |

| Event | Action | | | |
|---|---|---|--|---|
| | ET | IEC | ER | CONTRACTOR |
| sampling days at water sensitive receiver(s) | <ul style="list-style-type: none"> • If exceedance is found to be caused by the reclamation activities, repeat in-situ measurement to confirm findings; • Inform IEC and contractor; • Check monitoring data, all plant, equipment and Contractor's working methods; • Discuss mitigation measures with IEC and Contractor; • Ensure mitigation measures are implemented; • Prepare to increase the monitoring frequency to daily; • If exceedance occurs at WSD salt water intake, inform WSD; • Repeat measurement on next day of exceedance. | <ul style="list-style-type: none"> • Review proposal on mitigation measures submitted by Contractor and advise the ER accordingly; • Assess the effectiveness of the implemented mitigation measures. | <ul style="list-style-type: none"> • Assess the effectiveness of the implemented mitigation measures. | <ul style="list-style-type: none"> • Check all plant and equipment and consider changes of working methods; • Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; • Implement the agreed mitigation measures. |
| Limit level being exceeded by one sampling day at water sensitive receiver(s) | <ul style="list-style-type: none"> • Identify the source(s) of impact by comparing the results with those collected at the control stations as appropriate; | <ul style="list-style-type: none"> • Discuss with ET and Contractor on the mitigation measures; • Review proposal on mitigation measures submitted by Contractor and advise the ER accordingly; | <ul style="list-style-type: none"> • Discuss with IEC, ET and Contractor on the proposed mitigation measures; • Request Contractor to critically review the working methods; | <ul style="list-style-type: none"> • Inform the ER and confirm notification of the non-compliance in writing; • Rectify unacceptable practice; |

| Event | Action | | | |
|--|---|---|--|--|
| | ET | IEC | ER | CONTRACTOR |
| | <ul style="list-style-type: none"> • If exceedance is found to be caused by the reclamation activities, repeat <i>in-situ</i> measurement to confirm findings; • Inform IEC, contractor, AFCD and EPD • Check monitoring data, all plant, equipment and Contractor's working methods; • Discuss mitigation measures with IEC, ER and Contractor; • Ensure mitigation measures are implemented; • Increase the monitoring frequency to daily until no exceedance of Limit level; • If exceedance occurs at WSD salt water intake, inform WSD. | <ul style="list-style-type: none"> • Assess the effectiveness of the implemented mitigation measures. | <ul style="list-style-type: none"> • Make agreement on the mitigation measures to be implemented; • Assess the effectiveness of the implemented mitigation measures. | <ul style="list-style-type: none"> • Check all plant and equipment and consider changes of working methods; • Discuss with ET, IEC and ER and submit proposal of mitigation measures to IEC and ER within 3 working days of notification; • Implement the agreed mitigation measures. |
| Limit level being exceeded by two or more consecutive sampling days at | <ul style="list-style-type: none"> • Identify the source(s) of impact by comparing the results with those collected at the control stations as appropriate; | <ul style="list-style-type: none"> • Discuss with ET and Contractor on the mitigation measures; • Review proposal on mitigation measures submitted by Contractor and advise the ER accordingly; | <ul style="list-style-type: none"> • Discuss with IC(E), ET and Contractor on the proposed mitigation measures; • Request Contractor to critically review the working methods; | <ul style="list-style-type: none"> • Inform the ER and confirm notification of the non-compliance in writing; • Rectify unacceptable practice; |

| Event | Action | | | |
|-----------------------------|--|--|--|--|
| | ET | IEC | ER | CONTRACTOR |
| water sensitive receiver(s) | <ul style="list-style-type: none"> • If exceedance is found to be caused by the reclamation activities, repeat in-situ measurement to confirm findings; • Inform IC(E), AFCD, contractor and EPD; • Check monitoring data, all plant, equipment and Contractor's working methods; • Discuss mitigation measures with IC(E), ER and Contractor; • Ensure mitigation measures are implemented; • Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days; • If exceedance occurs at WSD salt water intake, inform WSD. | <ul style="list-style-type: none"> • Assess the effectiveness of the implemented mitigation measures. | <ul style="list-style-type: none"> • Make agreement on the mitigation measures to be implemented; • Assess the effectiveness of the implemented mitigation measures; • Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. | <ul style="list-style-type: none"> • Check all plant and equipment and consider changes of working methods; • Discuss with ET, IC(E) and ER and submit proposal of mitigation measures to IC(E) and ER within 3 working days of notification; • Implement the agreed mitigation measures; • As directed by the Engineer, to slow down or to stop all or part of the construction activities. |

Limit Levels and Action Plan for Landfill Gas

| Parameter | Limit Level | Action |
|----------------|----------------------------------|--|
| Oxygen | <19% | <ul style="list-style-type: none"> • Ventilate to restore oxygen to >19% |
| | <18% | <ul style="list-style-type: none"> • Stop works • Evacuate personnel/prohibit entry • Increase ventilation to restore oxygen to >19% |
| Methane | >10% LEL (i.e. > 0.5% by volume) | <ul style="list-style-type: none"> • Prohibit hot works • Ventilate to restore methane to <10% LEL |
| | >20% LEL (i.e. > 1% by volume) | <ul style="list-style-type: none"> • Stop works • Evacuate personnel / prohibit entry • Increase ventilation to restore methane to <10% LEL |
| Carbon Dioxide | >0.5% | <ul style="list-style-type: none"> • Ventilate to restore carbon dioxide to < 0.5% |
| | >1.5% | <ul style="list-style-type: none"> • Stop works • Evacuate personnel / prohibit entry • Increase ventilation to restore carbon dioxide to < 0.5% |

Event and Action Plan for Coral Post-Translocation Monitoring

| Event | Action | | | |
|--------------------------------|--|--|---|--|
| | ET Leader | IEC | ER | Contractor |
| Action Level Exceedance | 1. Check monitoring data; 2. Inform the IEC, ER and Contractor of the findings; 3. Increase the monitoring to at least once a month to confirm findings; 4. Propose mitigation measures for consideration | 1. Discuss monitoring with the ET and the Contractor; 2. Review proposals for additional Monitoring and any other measures submitted by the Contractor and advise the ER accordingly. | 1. Discuss with the IEC additional monitoring requirements and any other measures proposed by the ET; 2. Make agreement on the measures to be implemented. | 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the ER; 3. Implement the agreed measures. |
| Limit Level Exceedance | Undertake Steps 1-4 as in the Action Level Exceedance. If further exceedance of Limit Level, suspend construction works until an effective solution is identified. | 1. Discuss monitoring with the ET and the Contractor; 2. Review proposals for additional Monitoring and any other measures submitted by the Contractor and advise the ER accordingly. | 1. Discuss with the IEC additional monitoring requirements and any other measures proposed by the ET; 2. Make agreement on the measures to be implemented. | 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the ER; 3. Implement the agreed measures. |

Mitigation Measures for Vibration Monitoring

| Level | Contingency Action |
|-------------|--|
| Alert Level | <ul style="list-style-type: none"> ● The Engineer shall be informed immediately. ● The Contractor shall submit an investigation report to describe works being undertaken. To review the instrument responses and to study the cause of undue response. ● The Contractor shall review and increase the instrumentation monitoring and reporting frequency, if applicable. ● The Contractor shall submit a detailed plan of action describing the measures to be taken should the concerned instrument reach the action level to the Engineer for approval. |
| Alarm Level | <ul style="list-style-type: none"> ● The Engineer shall be informed immediately. ● The active construction works may require to be suspended subject to the Engineer's review of monitoring data. ● The Contractor shall immediately implement the measures as defined in the detailed plan of action to prevent further ground movement and groundwater drawdown etc. ● The Contractor shall prepare a detailed investigation report to study the cause of the exceedance ● The Contractor shall propose a contingency plan for the Engineer's approval in the event that alarm value is reached or exceeded ● The Contractor shall develop an emergency plan for the Engineer's approval in the event the applied contingency measures cannot control the situation. ● The Contractor shall meet the Engineer to discuss the instrument response and review the effectiveness of the implemented measures. ● The Contractor shall carry out design review of the works |

| | |
|--------------|--|
| Action Level | <ul style="list-style-type: none">● Consideration shall be given to suspend all active construction works and the Engineer shall be informed immediately● The Contractor shall immediately implement the measures defined in the contingency plan● The Contractor shall implement the measures defined in the emergency plan in the event that the applied contingency measures are found inadequate● The Contractor shall provide a complete report to examine the construction method and review the response of the instruments with full history of the monitoring data and construction activities and necessary design update● To resume the suspended activities, the Contractor shall demonstrate to the Engineer's satisfaction that it is safe to do so with approval from the Engineer. |
|--------------|--|

**APPENDIX N
ENVIRONMENTAL MITIGATION
IMPLEMENTATION SCHEDULE (EMIS)**

Table I – Recommended Mitigation Measures stipulated in EM&A Manual of the Project

(Further information on observations/reminders/non-compliance made during site audit should refer to Table II)

- Key:**
- ^ Mitigation measure was fully implemented.
 - * Observation/reminder was made during site audit but improved/rectified by the contractor.
 - # Observation/reminder was made during site audit but not yet improved/rectified by the contractor.
 - X Non-compliance of mitigation measure
 - Non-compliance but rectified by the contractor
 - N/A Not Applicable

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|---------------------------|--|---|--------------------------------|-----------------------------|---------------------------------|---|-----------------------------|
| Air Quality Impact | | | | | | | |
| S3.8.1 | Watering eight times a day on active works areas, exposed areas and paved haul roads | To minimize the dust impact | Contractor | All Active Work Sites | Construction phase | APCO | *(1)/#(1) |
| S3.8.1 | Enclosing the unloading process at barging point by a 3-sided screen with top tipping hall, provision of water spraying and flexible dust curtains | To minimize the dust impact | Contractor | Barging Points | Construction phase | APCO | N/A |
| S3.8.7 | Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices: <ul style="list-style-type: none"> - Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. - Use of frequent watering for particularly dusty construction areas and areas close to ASRs.h - Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be | To minimize the dust impact | Contractor | All Construction Work Sites | Construction phase | APCO and Air Pollution Control (Construction Dust) Regulation | *(1)/#(1) ^ ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|---------------------------------|---|--|
| | <p>applied to aggregate fines.</p> <ul style="list-style-type: none"> - Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. - Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations. - Establishment and use of vehicle wheel and body washing facilities at the exit points of the site. - Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading area of barging point, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods. - Provision of not less than 2.4m high hoarding from ground level along site boundary where adjoins a road, streets or other accessible to the public except for a site entrance or exit. - Imposition of speed controls for vehicles on site haul roads. - Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs - Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides. - Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise. | | | | | | <p>*(2)</p> <p>^</p> <p>N/A</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|--|---|---|--------------------------------|--------------------------|---------------------------------|---|----------------|
| / | Emission from Vehicles and Plants <ul style="list-style-type: none"> • All vehicles shall be shut down in intermittent use. • Only well-maintained plant should be operated on-site and plant should be serviced regularly to avoid emission of black smoke. • All diesel fuelled construction plant within the works areas shall be powered by ultra low sulphur diesel fuel (ULSD) | Reduce air pollution emission from construction vehicles and plants | Contractor | All construction sites | Construction stage | • APCO | ^ *(1) ^ |
| / | Valid No-road Mobile Machinery (NRMM) labels should be provided to regulated machines | Reduce air pollution emission from construction vehicles and plants | Contractor | All construction sites | Construction stage | • APCO | ^ |
| Noise Impact (Construction Phase) | | | | | | | |
| S4.8 | - Use of quiet PME. Use of movable noise barriers for Excavator, Lorry, Dump Truck, Mobile Crane, Compactor, Concrete Mixer Truck, Concrete Lorry Mixer, Breaker, Mobile Crusher, Backhoe, Vibratory Poker, Saw, Asphalt Paver, Vibratory Roller, Vibrolance, Hydraulic Vibratory Lance and Piling (Vibration Hammer). Use of full enclosure for Air Compressor, Compressor, Bar Bender, Generator, Drilling Rig, Chisel, Large Diameter Bore Piling, Grout Mixer & Pump and Concrete Pump. | To minimize construction noise impact arising from the Project at the affected NSRs | Contractor | Work Sites | Construction phase | EIAO-TM, NCO | N/A |
| Noise Mitigation Plan | Use of Temporary Noise Barriers or Full Enclosure for PME according to the approved Noise Mitigation Plan | To minimize construction noise impact arising from the Project at the affected NSRs | Contractor | Work Sites | Construction phase | EIAO-TM, NCO | *(3) |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|--|--|---|--------------------------------|--------------------------|---------------------------------|---|---------------------------------------|
| S4.9 | <p>Good Site Practice</p> <ul style="list-style-type: none"> - Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program - Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program. - Mobile plant, if any, should be sited as far away from NSRs as possible. - Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum. - Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. - Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities. | To minimize construction noise impact arising from the Project at the affected NSRs | Project Proponent | Work sites | Construction Period | EIAO-TM, NCO | ^ ^ ^ ^ ^ |
| S4.9 | Scheduling of Construction Works during School Examination Period | To minimize construction noise impact arising from the Project at the affected NSRs | Contractor | Work site near school | Construction phase | EIAO-TM, NCO | N/A |
| Water Quality Impact (Construction Phase) | | | | | | | |
| S5.6.24 | The dry density of filling material for the TKO-LT Tunnel reclamation should be 1,900kg/m ³ , with fine content of 25% or less | Control potential impacts from filling activities | CEDD's Contractors | Work site | Construction Phase | EIAO-TM, WPCO | N/A |
| S5.8.1 | Non-dredged method by constructing steel cellular caisson structure with stone column shall be adopted for construction of seawall foundation. During the stone column installation (also | Control potential impacts from filling | CEDD's Contractors | Work site | Construction Phase | EIAO-TM, WPCO | N/A |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|---|---|--------------------------------|--------------------------|---------------------------------|---|---|
| | including the installation of steel cellular caisson), silt curtain shall be employed around the active stone column installation points. | activities | | | | | |
| S5.8.2 | Formation of seawall enclosing the reclamation for Road P2 (notwithstanding an opening of about 50m for marine access) shall be completed prior to the filling activities. The seawall opening of about 50m wide for marine access shall be selected at a location as indicatively shown in Appendix 5.10. No more than 3 filling barge trips per day shall be made with a maximum daily rate of 3,000m ³ (i.e. 1,000 m ³ per trip) for the filling operation at the reclamation area for Road P2. All filling works shall be carried out behind the seawall with the use of single silt curtain at the marine access. | Control potential impacts from filling activities | CEDD's Contractors | Work site | Construction Phase | EIAO-TM, WPCO | N/A |
| S5.8.3 | <p>Other good site practices should be undertaken during filling operations include:</p> <ul style="list-style-type: none"> - all marine works should adopt the environmental friendly construction methods as far as practically possible including the use of cofferdams to cover the construction area to separate the construction works from the sea; - floating single silt curtain shall be employed for all marine works; - all vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; - all hopper barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material; - excess material shall be cleaned from the decks and exposed fittings of barges before the vessel is moved; - adequate freeboard shall be maintained on barges to reduce the likelihood of decks being washed by wave action; | Control potential impacts from filling activities and marine-based construction | CEDD's Contractors | Work site | Construction Phase | EIAO-TM, WPCO, Waste Disposal Ordinance (WDO) | <p>*(4)/#(4)</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|---------------|---|---|--------------------------------|--------------------------|---------------------------------|---|-------------------------------------|
| | <ul style="list-style-type: none"> - loading of barges and hoppers should be controlled to prevent splashing of filling material into the surrounding water. Barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation; - any pipe leakages shall be repaired quickly. Plant should not be operated with leaking pipes; - construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site or dumping grounds; and - before commencement of the reclamation works, the holder of Environmental Permit has to submit plans showing the phased construction of the reclamation, design and operation of the silt curtain. | | | | | | <p>^</p> <p>^</p> <p>^</p> <p>^</p> |
| S5.8.4 | Site specific mitigation plan for reclamation areas using public fill materials should be submitted for EPD agreement before commencement of construction phase with due consideration of good site practices. | Control potential impacts from filling activities and marine based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | N/A |
| ERR S5.6.1 | <p>To minimize water quality impact arising from the dredging and filling works for Reclamation for Road P2, the following mitigation measures shall be implemented:</p> <ul style="list-style-type: none"> - Before carrying out any dredging and underwater filling works, a temporary barrier shall first be constructed to a height above the high water mark to completely enclose the works site (without any opening at the barrier wall) - The temporary barrier fully enclosing the dredging and underwater filling works site shall not be removed before completion of all dredging and underwater filling works. - Water quality sampling and testing shall be carried out to demonstrate that the water | Control potential impacts from dredging and filling works for Reclamation for Road P2 | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | <p>^</p> <p>^</p> <p>N/A</p> |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|-------------------------------------|---|--------|
| | <p>quality inside the enclosed barrier is comparable to the ambient or baseline levels prior to the removal of the fully enclosed barrier.</p> <p>- Silt curtains shall be deployed for the installation and removal of the temporary barrier and at the double water gates marine access opening during its operation. The general of arrangement of silt curtain is shown in Figure 7 of the existing Environmental Permit (No. EP-458/2013/C).</p> | | | | | | ^ |
| S5.8.5 | It is important that appropriate measures are implemented to control runoff and drainage and prevent high loading of SS from entering the marine environment. Proper site management is essential to minimise surface water runoff, soil erosion and sewage effluents. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.6 | Any practical options for the diversion and realignment of drainage should comply with both engineering and environmental requirements in order to ensure adequate hydraulic capacity of all drains. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Design Stage and Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO, TM-DSS | ^ |
| S5.8.7 | Construction site runoff and drainage should be prevented or minimised in accordance with the guidelines stipulated in the EPD's Practice Note for Professional Persons, Construction Site Drainage (ProPECC PN 1/94). Good housekeeping and stormwater best management practices, as detailed in below, should be implemented to ensure that all construction runoff complies with WPCO standards and no unacceptable impact on the WSRs arises due to construction of the TKO-LT Tunnel. All discharges from the construction site should be controlled to comply with the standards for effluents discharged into the corresponding WCZ | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO, TM-DSS | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|---------------------------------|---|----------|
| | under the TM-DSS. | | | | | | |
| S5.8.8 | Exposed soil areas should be minimised to reduce the potential for increased siltation, contamination of runoff, and erosion. Construction runoff related impacts associated with the above ground construction activities can be readily controlled through the use of appropriate mitigation measures which include: - use of sediment traps; and - adequate maintenance of drainage systems to prevent flooding and overflow. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | N/A ^ |
| S5.8.9 | Construction site should be provided with adequately designed perimeter channel and pretreatment facilities and proper maintenance. The boundaries of critical areas of earthworks should be marked and surrounded by dykes or embankments for flood protection. Temporary ditches should be provided to facilitate runoff discharge into the appropriate watercourses, via a silt retention pond. Permanent drainage channels should incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.10 | Ideally, construction works should be programmed to minimise surface excavation works during the rainy season (April to September). All exposed earth areas should be completed as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.11 | Sedimentation tanks of sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8m ³ capacity, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity is flexible and | Control potential impacts from construction site | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|---------------------------------|---|--------|
| | able to handle multiple inputs from a variety of sources and particularly suited to applications where the influent is pumped. | runoff and land-based construction | | | | S5 | |
| S5.8.12 | Earthworks final surfaces should be well compacted and the subsequent permanent work or surface protection should be carried out immediately after the final surfaces are formed to prevent erosion caused by rainstorms. Appropriate drainage like intercepting channels should be provided where necessary. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO S5 | ^ |
| S5.8.13 | Measures should be taken to minimize the ingress of rainwater into trenches. If excavation of trenches in wet seasons is necessary, they should be dug and backfilled in short sections. Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO S5 | ^ |
| S5.8.14 | Open stockpiles of construction materials (for examples, aggregates, sand and fill material) of more than 50m ³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.15 | Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers. Discharge of surface runoff into foul sewers must always be prevented in order not to unduly overload the foul sewerage system. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|---------------------------------|---|--------|
| S5.8.16 | Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecast, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.17 | Oil interceptors should be provided in the drainage system and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | N/A |
| S5.8.18 | All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and located wheel washing bay should be provided at every site exit, and washwater should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheelwash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.19 | Silt removal facilities, channels and manholes should be maintained and the deposited silt and grit should be removed regularly, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES
October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|---------------------------------|---|--------|
| S5.8.20 | It is recommended that on-site drainage system should be installed prior to the commencement of other construction activities. Sediment traps should be installed in order to minimise the sediment loading of the effluent prior to discharge into foul sewers. There shall be no direct discharge of effluent from the site into the sea. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.21 | All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment control measures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage should be reinstated to its original condition when the construction work has finished or the temporary diversion is no longer required. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.22 | All fuel tanks and storage areas should be provided with locks and be located on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank, to prevent spilled fuel oils from reaching the coastal waters. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.23 | Minimum distances of 100m shall be maintained between the existing or planned stormwater discharges and the existing or planned seawater intakes during construction and operational phases | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | EIAO-TM, WPCO, TMDSS | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|--------------------------------|---|---|--------------------------------|--------------------------|------------------------------------|---|--------|
| S5.8.24 | Under normal circumstances, groundwater pumped out of wells, etc. for the lowering of ground water level in basement or foundation construction, and groundwater seepage pumped out of tunnels or caverns under construction should be discharged into storm drains after the removal of silt in silt removal facilities. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.25 - S5.8.27 & Table 5.18 | Grouting would be adopted as measure to reduce the groundwater inflow into the tunnel. During the tunnel excavation, the inflow rate of groundwater into the tunnel will be measured during the excavation. The groundwater levels above the tunnel will also be monitored by piezometers. If the inflow rate exceeds the pre-determined groundwater control criteria or the groundwater drawdown exceeds the required limit, pre-excavation grouting will be required to reduce the groundwater inflow. No significant change of groundwater levels would therefore be expected. Any chemicals/ foaming agents which would be entrained to the groundwater should be biodegradable and non-toxic throughout the tunnel construction. Potential groundwater quality impact would be minimal as the used material is non-toxic and biodegradable. No adverse groundwater quality would therefore be expected. Prescriptive measures in the form of an Action Plan with pre-emptive and re-active to preserve the groundwater levels at all times during the tunnel construction are set out in Table 5.18. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO, Buildings Ordinance | N/A |
| S5.8.28 | Water used in ground boring and drilling for site investigation or rock / soil anchoring should as far as practicable be recirculated after sedimentation. When there is a need for final disposal, the wastewater should be discharged into storm drains via silt removal facilities. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Design Stage and Construction Phas | ProPECC PN 1/94, EIAOTM, WPCO | N/A |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|-------------------|--|---|--------------------------------|--------------------------|---------------------------------|---|--------|
| S5.8.29 - S5.8.31 | Wastewater generated from the washing down of mixing trucks and drum mixers and similar equipment should whenever practicable be recycled. The discharge of wastewater should be kept to a minimum. To prevent pollution from wastewater overflow, the pump sump of any water recycling system should be provided with an online standby pump of adequate capacity and with automatic alternating devices. Under normal circumstances, surplus wastewater may be discharged into foul sewers after treatment in silt removal and pH adjustment facilities (to within the pH range of 6 to 10). Disposal of wastewater into storm drains will require more elaborate treatment. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.32 | All vehicles and plant should be cleaned before they leave a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. A wheel washing bay should be provided at every site exit if practicable and wash-water should have sand and silt settled out or removed before discharging into storm drains. The section of construction road between the wheel washing bay and the public road should be paved with backfall to reduce vehicle tracking of soil and to prevent site run-off from entering public road drains. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.33 | Bentonite slurries used in diaphragm wall and borepile construction should be reconditioned and reused wherever practicable. If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | N/A |
| S5.8.34 | If the used bentonite slurry is intended to be disposed of through the public drainage system, it should be treated to the respective effluent standards applicable to foul sewer, storm drains or the receiving waters as set out in the WPCO Technical Memorandum on Effluent Standards. | Control potential impacts from construction site runoff and land- | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | N/A |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|-------------------------------------|---|--------|
| | | based construction | | | | | |
| S5.8.35 | Water used in water testing to check leakage of structures and pipes should be reused for other purposes as far as practicable. Surplus unpolluted water could be discharged into storm drains. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | N/A |
| S5.8.36 | Sterilization is commonly accomplished by chlorination. Specific advice from EPD should be sought during the design stage of the works with regard to the disposal of the sterilizing water. The sterilizing water should be reused wherever practicable. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Design Stage and Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | N/A |
| S5.8.37 | Before commencing any demolition works, all sewer and drainage connections should be sealed to prevent building debris, soil, sand etc. from entering public sewers/drains. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | N/A |
| S5.8.38 | Wastewater generated from building construction activities including concreting, plastering, internal decoration, cleaning of works and similar activities should not be discharged into the stormwater drainage system. If the wastewater is to be discharged into foul sewers, it should undergo the removal of settleable solids in a silt removal facility, and pH adjustment as necessary | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|---------------------------------|---|--------|
| S5.8.39 | Acidic wastewater generated from acid cleaning, etching, pickling and similar activities should be neutralized to within the pH range of 6 to 10 before discharging into foul sewers. If there is no public foul sewer in the vicinity, the neutralized wastewater should be tinkered off site for disposal into foul sewers or treated to a standard acceptable to storm drains and the receiving waters | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.40 | Wastewater collected from canteen kitchens, including that from basins, sinks and floor drains, should be discharged into foul sewer via grease traps capable of providing at least 20 minutes retention during peak flow. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | N/A |
| S5.8.41 | Drainage serving an open oil filling point should be connected to storm drains via a petrol interceptor with peak storm bypass. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |
| S5.8.42 | Vehicle and plant servicing areas, vehicle wash bays and lubrication bays should as far as possible be located within roofed areas. The drainage in these covered areas should be connected to foul sewers via a petrol interceptor. Oil leakage or spillage should be contained and cleaned up immediately. Waste oil should be collected and stored for recycling or disposal in accordance with the Waste Disposal Ordinance. | Control potential impacts from construction site runoff and land-based construction | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | *(6) |
| S5.8.43 | Construction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage may need to be handled by portable chemical toilets prior to the commission of the on-site sewer system. | Control potential impacts from construction site | CEDD's Contractors | Work site | Construction Phase | ProPECC PN 1/94, EIAOTM, WPCO | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|---------------------------------|---|-------------|
| | Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor shall also be responsible for waste disposal and maintenance practices. | runoff and land-based construction | | | | | |
| S5.8.44 | Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes. | Control potential impacts from accidental spillage of chemicals | CEDD's Contractors | Work site | Construction Phase | EIAO-TM, WPCO, WDO | ^ |
| S5.8.45 | Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges. | Control potential impacts from accidental spillage of chemicals | CEDD's Contractors | Work site | Construction Phase | EIAO-TM, WPCO | *(7)/#(7) |
| S5.8.46 | <p>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The "Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes" published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows:</p> <ul style="list-style-type: none"> - suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport; - chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents; and - storage area should be selected at a safe location on site and adequate space should be allocated to the storage area. | Control potential impacts from accidental spillage of chemicals | CEDD's Contractors | Work site | Construction Phase | EIAO-TM, WPCO, WDO | ^ ^ ^ |
| S5.8.47 | Collection and removal of floating refuse should be performed at regular intervals on a daily basis. The contractor should be responsible for keeping the water within the site boundary | Control potential impacts from | CEDD's Contractors | Work site | Construction Phase | EIAO-TM, WPCO, | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|--------------------------|---|---|--------------------------------|--------------------------|---------------------------------|---|--|
| | and the neighbouring water free from rubbish. | floating refuse and debris | | | | | |
| Ecological Impact | | | | | | | |
| S6.8.4 | <p>Measures to Minimize Disturbance</p> <ul style="list-style-type: none"> - Use of Quiet Mechanical Plant during the construction phase should be adopted wherever possible. - Hoarding or fencing should be erected around the works area boundaries during the construction phase. The hoarding would screen adjacent habitats from construction phase activities, reduce noise disturbance to these habitats and also to restrict access to habitats adjacent to works areas by site workers; - Regular spraying of haul roads to minimize impacts of dust deposition on adjacent vegetation and habitats during the construction activities | Minimize noise, human and traffic disturbance to terrestrial habitat and wildlife; and reduce dust generation | Design Team / Contractor | Land-based works are | Construction Phase | N/A | ^ ^ ^ |
| S6.8.5 | <p>Standard Good Site Practice</p> <ul style="list-style-type: none"> - Placement of equipment or stockpile in designated works areas and access routes selected on existing disturbed land to minimise disturbance to natural habitats. - Construction activities should be restricted to works areas that should be clearly demarcated. The works areas should be reinstated after completion of the works. - Waste skips should be provided to collect general refuse and construction wastes. The wastes should be properly disposed off-site in a timely manner. - General drainage arrangements should include sediment and oil traps to collect and control construction site run-off. - Open burning on works sites is illegal, and should be strictly prohibited. - Measures should also be put into place so that litter, fuel and solvents do not enter the | Reduce disturbance to surrounding habitats | Contractor | Land-based works are | Construction Phase | N/A | #(5) ^ ^ #(5) ^ ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|---|---|---|---|---------------------------------|---|------------------------------|
| | nearby watercourses. | | | | | | |
| S6.8.6 | <p>Measure to Minimize Groundwater Inflow</p> <ul style="list-style-type: none"> - The drained tunnel construction method with groundwater inflow control measures would generally be adopted. - During the tunnel excavation, pre-excavation grouting could be adopted to reduce the groundwater inflow and ensure that the tunnel would meet the long term water tightness requirements. | Minimize groundwater inflow | Contractor | Tunnel | Construction Phase | N/A | N/A N/A |
| S6.8.8 | <p>Measure to Minimize Impact on Corals</p> <p><u>Coral translocation</u></p> <ul style="list-style-type: none"> - It is recommended to translocate the affected coral colonies, except the locally common <i>Oulastrea crispata</i>, within the reclamation area and bridge footprint to the other suitable locations as far as practicable. - The coral translocation should be conducted during the winter months (November-March) in order to avoid disturbance during their spawning period (i.e. July to October). - A detailed coral translocation plan with a description on the methodology for pretranslocation coral survey, translocation methodology, identification/proposal of coral recipient site, monitoring methodology for posttranslocation should be prepared during the detailed design stage. - The coral translocation plan should be subject to approval by relevant authorities (e.g. EPD and AFCD) before commencement of the coral translocation. All the translocation | Minimize loss of coral | Design team, contractor, project operator | Within reclamation areas and pier footprint | Prior construction | N/A | ^ ^ ^ ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|------------------------------|---|---|--------------------------------|--|---------------------------------|---|---------------------------------------|
| | <p>exercises should be conducted by experienced marine ecologist(s) who is/are approved by AFCD prior to commencement of coral translocation.</p> <p><u>Post translocation Monitoring</u></p> <ul style="list-style-type: none"> - A coral monitoring programme is recommended to assess any adverse and unacceptable impacts to the translocated coral communities - Information gathered during each posttranslocation monitoring survey should include observations on the presence, survival, health condition and growth of the translocated coral colonies. These parameters should then be compared with the baseline results collected from the pre-translocation survey. | | | | | | <p>^</p> <p>^</p> |
| <p>S6.8.9</p> <p>S6.8.10</p> | <p>Measure to Control Water Quality Impact</p> <ul style="list-style-type: none"> - Deployment of silt curtains around the active stone column installation points, opening of newly installed seawall and marine works area. - Diverting of the site runoff to silt trap facilities before discharging into storm drain; - Proper waste and dumping management; and - Standard good-site practice for land-based construction. | <p>Control water quality impact, especially on suspended solid level; minimize the contamination of wastewater discharge, accidental chemical spillage and construction site runoff to the receiving water bodies</p> | <p>Design Team, contractor</p> | <p>Marine and landbased works area</p> | <p>Construction phase</p> | <p>WQO</p> | <p>N/A</p> <p>^</p> <p>^</p> <p>^</p> |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|--|---|---|--------------------------------|--------------------------|---------------------------------|--|---------------------------------|
| S6.8.11 | <p>Compensation for Vegetation Loss</p> <ul style="list-style-type: none"> - Felling of mature trees should be compensated by planting of standard or heavy standard trees within or in vicinity of the affected area as far as practicable. Such compensatory planting for trees should be provided with at least a 1:1 ratio. In addition, vegetation at the temporarily affected area should be reinstated with species similar to the existing condition. | Compensate for the vegetation loss | Design Team, contractor | Land-based works area | Construction phase | N/A | ^ |
| Fisheries Impact | | | | | | | |
| S7.7.3 | <p>Measure to Control Water Quality Impact</p> <ul style="list-style-type: none"> - Deployment of silt curtains around the active stone column installation points, opening of newly installed seawall and marine works area. | Control water quality impact, especially on suspended solid level | Design Team / Contractor | Marine work area | Construction phase | WQO | ^ |
| Waste Management (Construction Phase) | | | | | | | |
| S8.6.3 | <p>Good Site Practices and Waste Reduction Measures</p> <ul style="list-style-type: none"> - Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; - Training of site personnel in site cleanliness, proper waste management and chemical handling procedures; - Provision of sufficient waste disposal points and regular collection of waste; - Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; and - Regular cleaning and maintenance programme for drainage systems, sumps and oil | To reduce waste management impacts | Contractor | All work sites | Construction Phase | Waste Disposal Ordinance (Cap. 354) Land (Miscellaneous Provisions) Ordinance (Cap. 28) | ^ ^ ^ *(8) |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|---------------------------------|--|------------------------------|
| | interceptors. | | | | | | |
| S8.6.4 | <p>Good Site Practices and Waste Reduction Measures (con't)</p> <ul style="list-style-type: none"> - Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; - Encourage collection of aluminium cans by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the workforce; - Proper storage and site practices to minimize the potential for damage or contamination of construction materials; and - Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste. | To achieve waste reduction | Contractor | All work sites | Construction Phase | Waste Disposal Ordinance (Cap. 354) Land (Miscellaneous Provisions) Ordinance (Cap. 28) | ^ ^ ^ ^ |
| S8.6.5 | <p>Good Site Practices and Waste Reduction Measures (con't)</p> <p>The Contractor shall prepare and implement a WMP as part of the EMP in accordance with ETWB TCW No. 19/2005 which describes the arrangements for avoidance, reuse, recovery, recycling, storage, collection, treatment and disposal of different categories of waste to be generated from the construction activities. Such a management plan should incorporate site specific factors, such as the designation of areas for segregation and temporary storage of reusable and recyclable materials. The EMP should be submitted to the Engineer for approval. The Contractor should implement the waste management practices in the EMP throughout the construction stage of the Project. The EMP should be reviewed regularly and updated by the Contractor.</p> | To achieve waste reduction | Contractor | All work sites | Construction Phase | ETWB TCW No. 19/2005 | ^ |
| S8.6.6 | <p>Good Site Practices and Waste Reduction Measures (con't)</p> <ul style="list-style-type: none"> - C&D materials would be reused in the project and other local concurrent projects as far as possible. | To achieve waste reduction | Contractor | All work sites | Construction Phase | ETWB TCW No. 19/2005 | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|---|--|--------------------------------|--------------------------|---------------------------------|---|----------------------------|
| S8.6.7 | <p><i>Storage, Collection and Transportation of Waste</i></p> <p>Should any temporary storage or stockpiling of waste is required, recommendations to minimize the impacts include:</p> <ul style="list-style-type: none"> - Waste, such as soil, should be handled and stored well to ensure secure containment, thus minimizing the potential of pollution; - Maintain and clean storage areas routinely; - Stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; and - Different locations should be designated to stockpile each material to enhance reuse. | To minimize potential adverse environmental impacts arising from waste storage | Contractor | All work sites | Construction Phase | - | ^ ^ ^ ^ |
| S8.6.8 | <p><i>Storage, Collection and Transportation of Waste (con't)</i></p> <ul style="list-style-type: none"> - Remove waste in timely manner; - Waste collectors should only collect wastes prescribed by their permits; - Impacts during transportation, such as dust and odour, should be mitigated by the use of covered trucks or in enclosed containers; - Obtain relevant waste disposal permits from the appropriate authorities, in accordance with the Waste Disposal Ordinance (Cap. 354), Waste Disposal (Charges for Disposal of Construction Waste) Regulation (Cap. 345) and the Land (Miscellaneous Provisions) Ordinance (Cap. 28); - Waste should be disposed of at licensed waste disposal facilities; and - Maintain records of quantities of waste generated, recycled and disposed. | To minimize potential adverse environmental impacts arising from waste collection and disposal | Contractor | All work sites | Construction Phase | | ^ ^ ^ ^ ^ ^ |
| S8.6.9 | <p><i>Storage, Collection and Transportation of Waste (con't)</i></p> <ul style="list-style-type: none"> - Implementation of trip ticket system with reference to DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials, to monitor disposal of | To minimize potential adverse environmental | Contractor | All work sites | Construction Phase | DEVB TCW No. 6/2010 | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|-------------------|---|--|--------------------------------|--|---------------------------------|---|---------------------|
| | waste and to control fly-tipping at PFRFs or landfills. A recording system for the amount of waste generated, recycled and disposed (including disposal sites) should be proposed. | impacts arising from waste collection and disposal | | | | | |
| S8.6.11 - S8.6.13 | <p>Sorting of C&D Materials</p> <ul style="list-style-type: none"> - Sorting to be performed to recover the inert materials, reusable and recyclable materials before disposal off-site. - Specific areas shall be provided by the Contractors for sorting and to provide temporary storage areas for the sorted materials. - The C&D materials should at least be segregated into inert and non-inert materials, in which the inert portion could be reused and recycled in the reclamation as far as practicable before delivery to PFRFs. While opportunities for reusing the non-inert portion should be investigated before disposal of at designated landfills | To minimize potential adverse environmental | Contractor | All work sites | Construction Phase | DEVB TCW No. 6/2010 ETWB TCW No. 33/2002 ETWB TCW No. 19/2005 | ^ ^ ^ |
| S8.6.15 – S8.6.16 | <p>Sediments</p> <ul style="list-style-type: none"> - Sediment encountered may be reused as filling material on-site after cement stabilization. Cement-stabilization process is undertaken by mixing sediment and cement and will convert sediment to earth filling material. The treated sediment has to comply with Risk-Based Remediation Goals (RBRGs) before being reused in order not to raise any land contamination issue. The adoption of RBRGs to assess stabilized sediment has been proposed in the current C&DMMP. MFC has no adverse comment on the current C&DMMP. The sediment quality indicates that all sediments comply with most stringent RBRGs except for one sediment sample (TKO-EBH501 3-3.95m) with lead exceeding the RBRG. Except for the sediment sample (TKO-EBH501 3-3.95m), the chemical screening | To ensure the sediment to be disposed of in an authorized and least impacted way | contractor | All works areas with sediments concern | Construction Phase | RBRG | N/A |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|-------------------|--|---|--------------------------------|--|---------------------------------|---|---------------------------|
| | <p>results do not indicate sediment as contaminated soil. It is anticipated that reuse of sediment except sediment sample (TKO-EBH501 3-3.95m) will not lead to land contamination.</p> <ul style="list-style-type: none"> - Despite exceedance of RBRG, onsite reuse of sediment under sample (TKO-EBH501 33.95m) as filling material after cement stabilization is also a suitable treatment. Sediment quality indicates the sediment sample (TKO-EBH501 3-3.95m) exceed RBRG for lead. While cement stabilization will immobilize metal contaminants, it is capable to treat the exceedance on lead. The stabilized material should comply with UTS of Lead and UCS. If the treated material do not comply with UTS or UCS, re-stabilization have to be undertaken to meet compliance of UTS and UCS before reusing the treated sediment as filling material. However, further agreement on final disposal/treatment on sediment under sample (TKO-EBH501 3-3.95m) has to be sought from DEP | | | | | | N/A |
| S8.6.17 – S8.6.20 | <p>Sediments (con't)</p> <ul style="list-style-type: none"> - Requirements of the Air Pollution Control (Construction Dust) Regulation, where relevant, shall be adhered to during boring, excavation, transportation and disposal of sediments or cement stabilization of sediment. - A treatment area should be confined for carrying out the cement stabilization mixing and temporary stockpile. The area should be designed to prevent leachate from entering the ground. Leachate, if any, should be collected and discharged according to the Water Pollution Control Ordinance (WPCO). - In order to minimise the potential odour / dust emissions during boring, excavation and transportation of the sediment, the excavated sediments should be kept wet during excavation/boring and should be properly covered when placed on barges/trucks. | To determine the best handling and treatment of sediment | Contractor | All works areas with sediments concern | Construction Phase | | N/A N/A N/A |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|-----------|--|--|--------------------------------|--|---------------------------------|---|--------|
| | <p>Loading of the excavated sediment to the barge should be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding water.</p> <ul style="list-style-type: none"> - In order to minimise the exposure to contaminated materials, workers should, when necessary, wear appropriate personal protective equipments (PPE) when handling contaminated sediments. Adequate washing and cleaning facilities should also be provided on site. | | | | | | N/A |
| S8.6.21 | <p>Sediments (con't)</p> <ul style="list-style-type: none"> - Alternatively, excavated sediment can be treated with marine disposal. The basic requirements and procedures for excavated sediment disposal specified under ETWB TC(W) No. 34/2002 shall be followed. MFC is responsible for the provision and management of disposal capacity and facilities for the excavated sediment, while the permit of marine dumping is required under the Dumping at Sea Ordinance and is the responsibility of the DEP. | To ensure the sediment to be disposed of in an authorized and least impacted way | contractor | All works areas with sediments concern | Construction Phase | ETWB TC(W) No. 34/2002 & Dumping at Sea Ordinance | N/A |
| S8.6.23 | <p>Sediments (con't)</p> <ul style="list-style-type: none"> - For allocation of sediment disposal sites and application of marine dumping permit, separate SSTP has to be submitted to EPD for agreement under DASO. Additional site investigation, based on the SSTP, maybe carried out in order to confirm the disposal arrangements for the proposed sediments removal. A Sediment Quality Report (SQR) shall then be required for EPD agreement under DASO prior to the tendering of the construction contract, discussing in details the site investigation, testing results as well as the delineation of each of the categories of excavated materials and the corresponding types of disposal. | To determine the best handling and disposal option of sediment | Contractor | All works areas with sediments concern | Construction Phase | ETWB TC(W) No. 34/2002 & Dumping at Sea Ordinance | N/A |
| S8.6.24 - | <p>Sediments (con't)</p> | To ensure handling | Contractor | All works | Construction | ETWB TC(W) No. | |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|---|---|--------------------------------|------------------------------|---------------------------------|---|---|
| S8.6.28 | <ul style="list-style-type: none"> - The excavated sediments is expected to be loaded onto the barge and transported to the designated disposal sites allocated by the MFC. The excavated sediment would be disposed of according to its determined disposal options and ETWB TC(W) No. 34/2002. - Stockpiling of contaminated sediments should be avoided as far as possible. If temporary stockpiling of contaminated sediments is necessary, the excavated sediment should be covered by tarpaulin and the area should be placed within earth bunds or sand bags to prevent leachate from entering the ground, nearby drains and surrounding water bodies. The stockpiling areas should be completely paved or covered by linings in order to avoid contamination to underlying soil or groundwater. Separate and clearly defined areas should be provided for stockpiling of contaminated and uncontaminated materials. Leachate, if any, should be collected and discharged according to the Water Pollution Control Ordinance (WPCO). - In order to minimise the potential odour / dust emissions during boring and transportation of the sediment, the excavated sediments should be kept wet during excavation/boring and should be properly covered when placed on barges. Loading of the excavated sediment to the barge should be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding water. - The barge transporting the sediments to the designated disposal sites should be equipped with tight fitting seals to prevent leakage and should not be filled to a level that would cause overflow of materials or laden water during loading or transportation. In addition, monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the DEP. | of sediments are in accordance to statutory requirements | | areas with sediments concern | Phase | 34/2002 & Dumping at Sea Ordinance | <p>N/A</p> <p>N/A</p> <p>N/A</p> <p>N/A</p> |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|---------------------------------|---|-----------------------|
| | <ul style="list-style-type: none"> - In order to minimise the exposure to contaminated materials, workers should, when necessary, wear appropriate personal protective equipments (PPE) when handling contaminated sediments. Adequate washing and cleaning facilities should also be provided on site. - Another possible arrangement for Type 3 disposal is by geosynthetic containment. A geosynthetic containment method is a method whereby the sediments are sealed in geosynthetic containers and, at the disposal site, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping, thereby meeting the requirements for fully confined mud disposal. | | | | | | <p>N/A</p> <p>N/A</p> |
| S8.6.26 | <p>Chemical Wastes.</p> <ul style="list-style-type: none"> - If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the Chemical Waste Treatment Centre at Tsing Yi, or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation. | To ensure proper management of chemical waste | Contractor | All works sites | Construction Phase | Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes Waste Disposal (Chemical Waste) (General) Regulation | ^ |
| S8.6.27 | General Refuse | To ensure proper | Contractor | All works sites | Construction | Public Health and | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES
October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|--|---|---|--------------------------------|--------------------------|----------------------------------|---|----------------------|
| | <ul style="list-style-type: none"> - General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material. | management of general refuse | | | Phase | Municipal Services Ordinance (Cap. 132) | |
| <i>Impact on Cultural Heritage (Construction Phase)</i> | | | | | | | |
| S9.6.4 | Dust and visual impacts <ul style="list-style-type: none"> - Temporarily fenced off buffer zone with allowance for public access (minimum 1 m) should be provided; - The open yard in front of the temple should be kept as usual for annual Tin Hau festival; - Monitoring of vibration impacts should be conducted when the construction works are less than 100m from the temple. | To prevent dust and visual impacts | Contractors | Work areas | Construction Phase | EIAO; GCHIA; AMO | ^ ^ ^ |
| S9.6.4 | Indirect vibration impact <ul style="list-style-type: none"> - Vibration level is suggest to be controlled within a peak particle velocity (ppv) limit of 5mm/s measured inside the historical buildings; - Monitoring of vibration should be carried out during construction phase. - Tilting and settlement monitoring should will be applied on the Cha Kwo Ling Tin Hau Temple as well. - A proposal with details for the mitigation measures and monitoring of impacts on built heritage shall be submitted to AMO for comments before commencement of work. | To prevent indirect vibration impact | Contractors | Work areas | Construction Phase | Vibration Limits on Heritage Buildings by CEDD; GCHIA; AMO. | ^ ^ ^ ^ |
| <i>Landscape and Visual Impact (Construction Phase)</i> | | | | | | | |
| Table 10.8.1 | CM1 - Construction area and contractor's temporary works areas to be minimised to avoid impacts on adjacent landscape. | Avoid impact on adjacent landscape areas | CEDD (via Contractor) | General | Construction planning and during | N/A | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES
October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|--------------|--|---|--------------------------------|---|---|--|--------|
| | | | | | construction period | | |
| Table 10.8.1 | CM2 - Reduction of construction period to practical minimum. | Minimise duration of impact | CEDD (via Contractor) | N/A | Construction planning | N/A | ^ |
| Table 10.8.1 | CM3 - Topsoil, where the soil material meets acceptable criteria and where practical, to be stripped and stored for re-use in the construction of the soft landscape works. The Contract Specification shall include storage and reuse of topsoil as appropriate. | To allow re-use of topsoil | CEDD (via Contractor) | General | Site clearance | As per the Particular Specification | ^ |
| Table 10.8.1 | CM4 - Existing trees at boundary of site and retained trees within site boundary to be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification, under which the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage). | To minimize tree loss | CEDD (via Contractor) | As per approved Tree Removal Application(s) | Site clearance and throughout construction period | ETWB TC 3/2006 and as per tree protection measures in Particular Specification | ^ |
| Table 10.8.1 | CM5 - Trees unavoidably affected by the works shall be transplanted where practicable. Where possible, trees should be transplanted direct to permanent locations rather than temporary holding nurseries. A detailed tree transplanting specification shall be provided in the Contract Specification and sufficient time for preparation shall be allowed in the construction programme. | To maximize preservation of existing trees | CEDD (via Contractor) | As per approved Tree Removal Application(s) | Site clearance | ETWB TC 3/2006 and as per tree protection measures in Particular Specification | ^ |
| Table 10.8.1 | CM6 - Advance screen planting of fast growing tree and shrub species to noise barriers and hoardings. Trees shall be capable of reaching a height >10m within 10 years. | To maximize screening of the works | CEDD (via Contractor) | At Lam Tin Interchange and edge of Road P2 | Beginning of construction period | N/A | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES
October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|--------------|---|---|--------------------------------|--|---------------------------------------|---|--------|
| | | | | landscape deck, TKO | | | |
| Table 10.8.1 | CM7 - Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material | To reduce visual intrusion | CEDD (via Contractor) | General | Throughout construction period | As per Particular Specification | N/A |
| Table 10.8.1 | CM8 - Control of night-time lighting by hooding all lights and through minimisation of night working periods. | To reduce visual intrusion | CEDD (via Contractor) | General | Throughout construction period | N/A | ^ |
| Table 10.8.1 | CM9 - Screening of works areas with hoardings with appropriate colours compatible with the surrounding area | Reduction of visual intrusion | CEDD (via Contractor) | Project site Boundary | Excretion of site hoarding | N/A | ^ |
| Table 10.8.1 | CM10 - Avoidance of excessive height and bulk of site buildings and structure | Reduction of visual intrusion and integration with environment | CEDD (via Contractor) | Built structures | Design and construction stage | N/A | ^ |
| Table 10.8.1 | CM11 - Limitation of run-off into freshwater streams, ponds and sea areas | Avoidance of contamination of water courses and water bodie | CEDD (via Contractor) | TKO reclamation, TKO tunnel portal, Cha Kwo Ling roadworks | Throughout construction period | N/A | ^ |
| Table 10.8.1 | CM12 - Minimise area of reclamation and design the edges sensitively to tie in with adjacent coastline characte | Minimise loss of Junk Bay and integration with | CEDD (via Contractor) | Temporary reclamation for barging | Construction planning and reclamation | N/A | N/A |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|--|--|---|--------------------------------|--|---------------------------------|---|--------|
| | | existing coastlin | | points at TKO and Lam Tin and permanent reclamation for TKO Interchange slip roads and Road P2 | stages | | |
| Landfill Gas Hazard (Design and Construction Phase) | | | | | | | |
| S11.5.9 | <p>A Safety Officer, trained in the use of gas detection equipment and landfill gas-related hazards, should be present on site throughout the groundworks phase. The Safety Officer should be provided with an intrinsically safe portable instrument, which is appropriately calibrated and able to measure the following gases in the ranges indicated below:</p> <p>Methane 0-100% LEL and 0100% v/v</p> <p>Carbon dioxide 0-100%</p> <p>Oxygen 0-21%</p> | Protect the workers from landfill gas hazards | Contractor | Project sites within the Sai Tso Wan Landfill Consultation Zone | Construction phase | EPD's Landfill Gas Hazard Assessment Guidance Note | ^ |
| S11.5.10 S11.5.25 | <p>Safety Measures</p> <p>- For staff who work in, or have responsibility for “at risk” area, such as all excavation workers, supervisors and engineers working within the Consultation Zone, should receive appropriate training on working in areas susceptible to landfill gas, fire and explosion hazards.</p> | Protect the workers from landfill gas hazards | Contractor | Project sites within the Sai Tso Wan Landfill Consultation | Construction phase | EPD's Landfill Gas Hazard Assessment Guidance Note Labour | ^ |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|---|---|--------------------------------|--------------------------|---------------------------------|---|--|
| | <ul style="list-style-type: none"> - An excavation procedure or code of practice to minimize landfill gas related risk should be devised and carried out. - No worker should be allowed to work alone at any time in or near to any excavation. At least one other worker should be available to assist with a rescue if needed. - Smoking, naked flames and all other sources of ignition should be prohibited within 15m of any excavation or ground-level confined space. “No smoking” and “No naked flame” notices should be posted prominently on the construction site and, if necessary, special areas should be designed for smoking. - Welding, flame-cutting or other hot works should be confined to open areas at least 15m from any trench or excavation. - Welding, flame-cutting or other hot works may only be carried out in trenches or confined spaces when controlled by a “permit to work” procedure, properly authorized by the Safety Officer (or, in the case of small developments, other appropriately qualified person). - The permit to work procedure should set down clearly the requirements for continuous monitoring for methane, carbon dioxide and oxygen throughout the period during which the hot works are in progress. The procedure should also require the presence of an appropriately qualified person, in attendance outside the 'confined area', who should be responsible for reviewing the gas measurements as they are made, and who should have executive responsibility for suspending the work in the event of unacceptable or hazardous conditions. Only those workers who are appropriately trained and fully aware of the potentially hazardous conditions which may arise should be permitted to carry out hot works in confined areas. | | | Zone | | Department's Code of Practice for Safety and Health at Work in Confined Space | <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|--|---|--------------------------------|--------------------------|---------------------------------|---|--|
| | <ul style="list-style-type: none"> - Where there are any temporary site offices, or any other buildings located within the Sai Tso Wan Landfill Consultation Zone which have enclosed spaces with the capacity to accumulate landfill gas, then they should either be located in an area which has been proven to be free of landfill gas (by survey using portable gas detectors); or be raised clear of the ground by a minimum of 500mm. This aims to create a clear void under the structure which is ventilated by natural air movement such that emission of gas from the ground are mixed and diluted by air. - Any electrical equipment, such as motors and extension cords, should be intrinsically safe. During piping assembly or conduiting construction, all valves/seals should be closed immediately after installation. As construction progresses, all valves/seals should be closed to prevent the migration of gases through the pipeline/conduit. All piping /conduiting should be capped at the end of each working day. - During construction, adequate fire extinguishing equipment, fire-resistant clothing and breathing apparatus (BA) sets should be made available on site. - Fire drills should be organized at not less than six monthly intervals. - The contractor should formulate a health and safety policy, standards and instructions for site personnel to follow. - All personnel who work on the site and all visitors to the site should be made aware of the possibility of ignition of gas in the vicinity of excavations. Safety notices (in Chinese and English) should be posted at prominent position around the site warning danger of the potential hazards. - Service runs within the Consultation Zone should be designated as "special routes"; utilities companies should be informed of this and precautionary measures should be | | | | | | <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|------------------------------------|---|---|--------------------------------|--|---------------------------------|---|-------------------|
| | <p>implemented. Precautionary measures should include ensuring that staff members are aware of the potential hazards of working in confined spaces such as manholes and service chambers, and that appropriate monitoring procedures are in place to prevent hazards due to asphyxiating atmospheres in confined spaces. Detailed guidance on entry into confined spaces is given in Code of Practice on Safety and Health at Work in Confined Spaces (Labour Department, Hong Kong).</p> <ul style="list-style-type: none"> - Periodically during ground-works construction within the 250m Consultation Zone, the works area should be monitored for methane, carbon dioxide and oxygen using appropriately calibrated portable gas detection equipment. The monitoring frequency and areas to be monitored should be set down prior to commencement of ground-works either by the Safety Officer or an approved and appropriately qualified person. | | | | | | ^ |
| <p>S11.5.26 - S11.5.31</p> | <p>Monitoring</p> <ul style="list-style-type: none"> ● Routine monitoring should be carried out in all excavations, manholes, chambers, relocation of monitoring wells and any other confined spaces that may have been created. All measurements in excavations should be made with the extended monitoring tube located not more than 10 mm from the exposed ground surface. Monitoring should be performed properly to make sure that the area is free of landfill gas before any man enters into the area. ● For excavations deeper than 1m, measurements should be carried out: <ul style="list-style-type: none"> - at the ground surface before excavation commences;- - immediately before any worker enters the excavation; - at the beginning of each working day for the entire period the excavation remains open; <p>and</p> | <p>Protect the workers from landfill gas hazards</p> | <p>Contractor</p> | <p>Project sites within the Sai Tso Wan Landfill Consultation Zone</p> | <p>Construction phase</p> | <p>EPD's Landfill Gas Hazard Assessment Guidance Note</p> | <p>^</p> <p>^</p> |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| EIA Ref. | Recommended Mitigation Measures | Objectives of the recommended Measures & Main Concerns to address | Who to implement the measures? | Location of the measures | When to Implement the measures? | What requirements or standards for the measures to achieve? | Status |
|----------|---|---|--------------------------------|--|---------------------------------|---|---|
| | <ul style="list-style-type: none"> - periodically throughout the working day whilst workers are in the excavation. ● For excavations between 300mm and 1m deep, measurements should be carried out: <ul style="list-style-type: none"> - directly after the excavation has been completed; and - periodically whilst the excavation remains open. ● For excavations less than 300mm deep, monitoring may be omitted, at the discretion of the Safety Officer or other appropriately qualified person. ● Depending on the results of the measurements, actions required will vary and should be set down by the Safety Officer or other appropriately qualified person. ● The exact frequency of monitoring should be determined prior to the commencement of works, but should be at least once per day, and be carried out by a suitably qualified or qualified person before starting the work of the day. Measurements shall be recorded and kept as a record of safe working conditions with copies of the site diary and submitted to the Engineer for approval. The Contractor may elect to carry out monitoring via an automated monitoring system. | | | | | | <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> |
| S11.5.32 | <p>The hazards from landfill gas during the construction stage within the Sai Tso Wan Landfill Consultation Zone should be minimized by suitable precautionary measures recommended in Chapter 8 of the Landfill Gas Hazard Assessment Guidance Note.</p> | <p>construction stage within the Sai Tso Wan</p> <p>Protect the workers from landfill gas hazards</p> | Contractor | <p>Project sites within the Sai Tso Wan Landfill Consultation Zone</p> | Construction phase | <p>EPD's Landfill Gas Hazard Assessment Guidance Note</p> | N/A |

Table II - Observations/reminders/non-compliance made during Site Audit

- Key:**
- * Observation/reminder was made during site audit but improved/rectified by the contractor.
 - # Observation/reminder was made during site audit but not yet improved/rectified by the contractor.
 - X Non-compliance of mitigation measure
 - Non-compliance but rectified by the contractor

| Status / Remark | EIA Ref. | Recommended Mitigation Measures | Contract No. | Work Sites | Details of Observation/Reminder |
|---------------------------|----------|---|--------------|-------------------------------------|---|
| Air Quality Impact | | | | | |
| * (1) | S3.8.1 | Watering eight times a day on active works areas, exposed areas and paved haul roads | NE/2015/01 | Construction of Lam Tin Interchange | Water spraying should be provided to breaking works at Slope F at Lam Tin Interchange for dust suppression. |
| | S3.8.7 | Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices: <ul style="list-style-type: none"> - Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. - Use of frequent watering for particularly dusty construction areas and areas close to ASRs. - Only well-maintained plant should be operated on-site and plant should be serviced regularly to avoid emission of black smoke. | NE/2015/01 | Construction of Lam Tin Interchange | Dust screens should be erected at Portion 6 at TKO to reduce fugitive emission. |
| | | | NE/2015/01 | Construction of Lam Tin Interchange | Dark smoke emitted from generator at LTI should be avoided. |
| # (1) | | | NE/2015/01 | Construction of Lam Tin Interchange | Water spraying should be provided more frequently at LTI for dust suppression. |
| * (2) | S3.8.7 | Dust suppression measures stipulated in the Air Pollution Control (Construction | NE/2015/02 | Construction of | The Contractor was reminded to cover the open stockpiles |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| Status / Remark | EIA Ref. | Recommended Mitigation Measures | Contract No. | Work Sites | Details of Observation/Reminder |
|--|-----------------------|---|--------------|-------------------------------------|--|
| | | Dust) Regulation and good site practices: - Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. | | Road P2 | of dusty materials in Work Area A. |
| Noise Impact (Construction Phase) | | | | | |
| * (3) | Noise Mitigation Plan | Use of Temporary Noise Barriers or Full Enclosure for PME according to the approved Noise Mitigation Plan | NE/2015/01 | Construction of Lam Tin Interchange | Noise barriers at Portion IVC should be erected to reduce noise nuisance to nearby NSRs. |
| | | | NE/2015/02 | Construction of Road P2 | The Contractor was reminded to erect noise barrier properly before commencement of work in Portion 4 to reduce noise nuisance. |
| Water Quality Impact (Construction Phase) | | | | | |
| * (4) | S5.8.3 | all marine works should adopt the environmental friendly construction methods as far as practically possible including the use of cofferdams to cover the construction area to separate the construction works from the sea; | NE/2015/01 | Construction of TKO Portal | The Contractor was reminded to extend the geotextile of silt curtain to the seabed at TKO site to prevent silty discharge. |
| # (4) | | | NE/2015/02 | Construction of Road P2 | The Contractor was reminded to provide bunds to the gaps found at the edge of double water gate's deck so as to prevent the escape of materials into the surrounding waters. |
| # (5) | S6.8.5 | Standard Good Site Practice - Placement of equipment or stockpile in designated works areas and access routes selected on existing disturbed land to minimise disturbance to natural habitats. - General drainage arrangements should include sediment and oil traps to collect and control construction site run-off. | NE/2015/02 | Construction of Road P2 | The Contractor was reminded to clear the accumulated silt & sediment in the ditch near the site entrance regularly. |
| | | | NE/2015/02 | Construction of Road P2 | Stockpiles of dusty material were observed in the steel tanks (the west of Type 2 cofferdam). The Contractor should provide preventive measures to avoid overflow of dusty material. |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| Status / Remark | EIA Ref. | Recommended Mitigation Measures | Contract No. | Work Sites | Details of Observation/Reminder |
|--|----------|--|--------------|-------------------------------------|--|
| * (6) | S 5.8.42 | Vehicle and plant servicing areas, vehicle wash bays and lubrication bays should as far as possible be located within roofed areas. The drainage in these covered areas should be connected to foul sewers via a petrol interceptor. Oil leakage or spillage should be contained and cleaned up immediately. Waste oil should be collected and stored for recycling or disposal in accordance with the Waste Disposal Ordinance. | NE/2015/01 | Construction of Lam Tin Interchange | Oil stains at Portion IVC should be properly disposed of as chemical waste. |
| * (7) | S5.8.45 | Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. | NE/2015/01 | Construction of TKO Portal | Drip tray should be provided to chemical containers at Portion IVC. |
| # (7) | | Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges. | NE/2015/01 | Construction of TKO Portal | Drip tray should be provided to air compressors at Portion 6 at TKO site. |
| Waste Management (Construction Phase) | | | | | |
| * (8) | S8.6.3 | Good Site Practices and Waste Reduction Measures - Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. | NE/2015/01 | Construction of TKO Portal | The Contractor was reminded to treat site runoff at TKO site with wastewater treatment facility below the BMCPD pathway before discharge |
| | | | NE/2015/02 | Construction of Road P2 | Stagnant water was observed in drip trays at Portion 8 near the worker's rest area, the Contractor was reminded to clear stagnant water regularly. |

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

October 2017

| Status / Remark | EIA Ref. | Recommended Mitigation Measures | Contract No. | Work Sites | Details of Observation/Reminder |
|--------------------|----------|---------------------------------|--------------|---|---|
| | | | NE/2015/03 | Construction of Northern Footbridge | Water is accumulated in the drip tray of the generator at East Pier. The Contractor is reminded to clean up regularly and properly. |

**APPENDIX O
SUMMARIES OF ENVIRONMENTAL
COMPLAINT, WARNING, SUMMON
AND NOTIFICATION OF SUCCESSFUL
PROSECUTION**

Appendix O - Cumulative Log for Complaints, Notifications of Summons and Successful Prosecutions**Cumulative Complaint Log for Tseung Kwan O - Lam Tin Tunnel**

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|-------------------------------|---|---|---------------------|--|-------------------------------------|---|-------------|
| 1 | 7 th December 2016 | Not Specified / construction of Lam Tin Interchange | Resident of Yau Lai Estate Bik Lai House | Air Quality & Noise | The complainant complained about the construction noise and dust near Yau Lai Estate. (EPD Reference No.: K15/RE/00032001-16) | Y | According to information provided by the Contractor, powered Mechanical Equipment being operated for construction of Lam Tin Interchange on 7 and 9 December 2016 include breaker, dump truck, backhoes, drilling rig and small bulldozer. They were operated on and off with some idling time. It is considered that noise nuisance during the time of complaint was mainly due to high noise level emission during the use of breaker for rock breaking. The Contractors had implemented environmental mitigation measures in accordance with the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual to reduce construction dust and noise nuisance to the vicinity. | Closed |
| 2 | 9 th December 2016 | Not Specified / construction of Lam Tin Interchange | Resident of Yau Lai Estate Block A Nga Lai House | Noise | The complainant complained about the construction noise near Yau Lai Estate. (EPD Reference No.: K15/RE/00032317-16) | Y | According to the regular air quality monitoring conducted at Air Quality Monitoring Stations AM3, no Action or Limit Level Exceedance was recorded from 6 – 14 December 2016. Similarly, no Limit Level Exceedance was recorded at Noise Monitoring Station CM1, Station CM2 and Station CM3 from 6 – 16 December 2016. With the implementation of environmental mitigation measures by Contractor on site, it is considered that no adverse air quality and noise impact was brought to the nearby sensitive receivers by the works of this Project. | Closed |
| 3 | 9 th December 2016 | Not Specified / Construction of Road P2 | Sai Kung District Council Member Mr. Chan Kai Wai | Air Quality & Noise | The complainant complained about the noise nuisance during transportation of construction materials on haul road and dust generation during construction activities. | Y | No construction activities were carried out for both construction of Road P2 and TKO portal during night time or at about 7am. Therefore, no construction noise nuisance were generated during night-time or at about 7am under this Project and it is considered that these noise nuisance is not project- related. The Contractors of this Project had implemented environmental mitigation measures for air quality, noise and visual impact (night-time lighting) in accordance with the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual. | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|--------------------------------|---|-----------------------------------|--------|--|-------------------------------------|---|-------------|
| 4 | 20 th December 2016 | Not Specified / Construction of Road P2 | Resident of Ocean Shore | Noise | The complainant complained about the lighting and noise nuisance on construction vessels moored near Ocean Shores during night time. | Y | <p>The Contractors had taken the initiative to provide additional noise mitigation measures to works since the complaints were received including:</p> <ul style="list-style-type: none"> - Temporary noise barrier had been installed to reduce noise nuisance from piling works in construction of Road P2 - Provision of noise enclosure to cover generators for reducing its noise nuisance in TKO portal; and - Provision of portable noise enclosures at breakers and generators to reduce noise emission from works in TKO portal <p>According to the regular air quality and noise monitoring for this Project, no Action or Limit Level Exceedance was recorded in December 2016. With the implementation of environmental mitigation measures by Contractors on site, it is considered that no adverse air quality and noise impact was brought to the nearby sensitive receivers by the works of this Project.</p> <p>According to the ET's ad-hoc site inspection during night-time, no unacceptable noise nuisance from this Project was heard. No strong light emission from all the construction vessels near Ocean Shores was observed yet minimum lighting for marine safety purpose was observed from the construction vessel and anchors.</p> | Closed |
| 5 | 22nd December 2016 | 21 Dec 2016 at night / Construction of TKO portal | Resident of Block 3, Ocean Shores | Noise | The complainant concerned the noise generated by the construction works at hillside near Block 3 of Ocean Shores in daytime. | Y | | Closed |
| 6 | 22nd December 2016 | Not specified / Construction of TKO portal | Public | Noise | The complainant complained about the noise generated by the construction works at hillside in daytime. | Y | | Closed |
| 7 | 22nd December 2016 | Not specified / Construction of Road P2 | Resident from Ocean Shore | Noise | The complainant complained about the noise nuisance of broadcast on construction vessel near Ocean Shores at 7am and the noise generated by the construction works outside Tseung Kwan O Chinese Permanent Cemetery. | Y | | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|--------------------------------|--|---------------------------|-----------------|---|-------------------------------------|--|-------------|
| 8 | 22 nd December 2016 | Not specified / Construction of Road P2 and TKO portal | Resident from Ocean Shore | Noise | The complainant complained about the noise nuisance generated by construction works of Tseung Kwan O portal in daytime and noise nuisance of “loud speaker” on construction vessel near Ocean Shores. | Y | | Closed |
| 9 | 16 th December 2016 | Not Specified / near Ocean Shores | DC member | Noise & (Light) | The complainant complained that they noticed about 2 work vessels were being used at 00:00-01:00 and also moored there overnight which caused light pollution and affecting the residents. | Y | <p>According to the findings of investigation, minimum lighting on the construction vessel was required for guard watching the works site. Adverse night-time light and noise nuisance from the marine works area near Ocean Shores as alleged by the complainant are considered not caused by this Project.</p> <p>The Contractor had continuously implemented environmental mitigation measures in accordance with the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual. To avoid strong light emission towards the sensitive receivers, night-time lighting is properly controlled by hooding all lights (except necessary lighting for safety purpose and guard watching);</p> | Closed |
| 10 | 17 th January 2017 | 5 January 2017 / near Ocean Shores | DC member | Noise & (Light) | The complainant complained that marine vessels were used at about 22:00 and around 01:00 on 5 Jan 2017, again causing noise and light nuisance to the residents. | Y | <p>According to the ET’s ad-hoc site inspection during night-time, no unacceptable noise nuisance from this Project was heard. No strong light emission from all the construction vessels near Ocean Shores was observed yet minimum lighting for marine safety and guard watching purpose was observed from the construction vessel and anchors.</p> <p>The Contractor was recommended to continuously implement the following visual impact mitigation measures:</p> <ul style="list-style-type: none"> • necessary lighting on construction vessels should be oriented as much as possible such that direct strong lighting towards the sensitive receivers is avoided. • Strong lighting that may be in intermittent use should be shut down between works periods | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|--------------------------------|--|--|--------|--|-------------------------------------|--|-------------|
| 11 | 23 rd December 2016 | Not Specified / near Cha Kwo Ling Tsuen | Cha Kwo Ling Tsuen | Water | The complainant complaint about the Soil/muddy water from construction site near Cha Kwo Ling Tsuen. (EPD Reference No.: K15/RE/00033951-16) | N | No construction works were being carried out on 23 rd December 2016 at Portion WA1, which is the site portion near Cha Kwo Ling Tsuen. Despite, it was recorded that some muddy water was flowing from the Contractor's wheel washing facility to the gullies within the site boundary. | Closed |
| 12 | 29 th December 2016 | 23 rd December 2016 / near Cha Kwo Ling Tsuen | Cha Kwo Ling Tsuen | Water | The complainant complaint that some muddy water flowing from the wheel washing facility to the gullies within the site boundary. | N | For complaint of muddy water on 23 rd December 2016, the Contractor has fixed the clear water hose for wheel washing on 24 th December 2016 early morning. During the recent weekly site inspections to Site Portion WA1, no muddy water was observed leaked out of the Site Boundary. | Closed |
| 13 | 6 th January 2017 | Not Specified / construction of Lam Tin Interchange | Resident of Yau Lai Estate Block A Nga Lai House | Noise | The complainant complained about the noise nuisance during rock breaking at the Eastern Harbour Crossing (EHC) portal and lack of noise mitigation measures during the construction works. | Y | After investigation, it was found out that necessary rock breaking works by hydraulic or pneumatic breakers was conducted during excavation for tunnel adit at Lam Tin Interchange. Noise nuisance from the works area is considered due to the high noise level emission during use of hydraulic or pneumatic breakers. The Contractor had implemented environmental mitigation measures in accordance with the "Implementation Schedule of Proposed Mitigation Measures" of EM&A Manual as below: <u>Air Quality</u> Use of frequent watering during construction of Lam Tin Interchange, including watering of eight times a day on active work area, exposed area and paved haul roads to mitigate air quality impacts to the nearby Air Sensitive Receivers (ASRs) | Closed |
| 14 | 6 th January 2017 | Not Specified / Cha Kwo Ling Road | Resident of Yau Lai Estate | Noise | The complainant complained about the noise nuisance generated by the excavation works at Cha Kwo Ling Road on 6 January 2017 just after 7 a.m. | Y | <u>Noise</u> ● Provision of portable noise enclosures to head of breakers to reduce noise emission during rock breaking works in Lam Tin | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|-------------------------------|---|--|---------------------|---|-------------------------------------|---|-------------|
| 15 | 6 th January 2017 | Not Specified / Construction site near Yau Lai Estate | Resident of Yau Lai Estate Bik Lai House | Air Quality & Noise | The complainant complained about the noise nuisance during the construction works near Yau Lai Estate at 7:15am. He requested to erect noise barriers and set up water spraying system to minimize the noise and air nuisances to the nearby residents. | Y | Interchange; <ul style="list-style-type: none"> ● Provision of portable noise enclosures to reduce noise nuisance from drilling works and generator in Lam Tin Interchange; and ● Use of Quiet PME on-site including generator and hydraulic excavator. <p>The Contractor has taken the initiative to implement additional noise mitigation measures in order to further minimize noise nuisance to the nearby sensitive receivers, including the followings:</p> <ul style="list-style-type: none"> ● Provision and installation of additional temporary noise barrier during rock breaking works for construction of Lam Tin Interchange; ● Commencement time of daily construction works for construction of Lam Tin Interchange has been postponed from 7am to 8am each day. | Closed |
| 16 | 6 th January 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Yau Lai Estate Cheuk Lai House | Noise | The complainant complained the construction noise generated from this Project (EPD Reference No.: K15/RE/00000564-17) | Y | According to the regular air quality and noise monitoring for this Project, no Action or Limit Level Exceedance was recorded from 16 December 2016 to 19 January 2017. With the implementation of environmental mitigation measures by Contractors on site, it is considered that no adverse air quality and noise impact was brought to the nearby sensitive receivers by the works of this Project. | Closed |
| 17 | 6 th January 2017 | Not Specified / Construction site near Yau Lai Estate | Resident of Yau Lai Estate Bik Lai House | Noise | The Yau Lai Estate Property Services Management Office mentioned that one of the resident of Yau Lai Estate had complained to Hong Kong Housing Authority (HKHA) about the noise generated by the construction works. | Y | Nevertheless, the Contractor was recommended to continue to properly implement and strictly follow the air quality and noise mitigation measures as recommended in the Environmental Monitoring & Audit Manual and approved Noise Mitigation Plan to minimize environmental impact on the construction site. | Closed |
| 18 | 10 th January 2017 | Not Specified | Anonymous | Noise | The complainant complained the construction noise generated from this Project (EPD Reference | Y | | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|-------------------------------|--|--|--------|--|-------------------------------------|----------------------------------|-------------|
| | | | | | No.: K15/RE/0000967-17) | | | |
| 19 | 12 th January 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Yau Lai Estate | Noise | The complainant complained the noise generated from rock breaking at Lam Tin Interchange. He requested concrete actions to improve the situation. | Y | | Closed |
| 20 | 12 th January 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Yau Lai Estate Bik Lai House | Noise | The complainant complained the noise generated from rock breaking at Lam Tin Interchange. | Y | | Closed |
| 21 | 13 th January 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Yau Lai Estate Bik Lai House | Noise | The complainant complained the construction noise generated at Lam Tin Interchange at 7am in the morning. | Y | | Closed |
| 22 | 13 th January 2017 | Not Specified / Construction Works near Eastern Harbour Crossing tunnel portal | Anonymous | Noise | The complainant complained about the noise generated by the construction works near the toll plaza of the Eastern Harbour Crossing (EHC). The complainant complained again on 24 Jan 2017 and mentioned the noise problem still affected the daily life of residents | Y | | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|-------------------------------|--|--|--------|--|-------------------------------------|---|-------------|
| 23 | 16 th January 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Yau Lai Estate | Noise | The complainant complained the construction noise generated at Lam Tin Interchange at 7am in the morning. | Y | | Closed |
| 24 | 17 th January 2017 | Not Specified / construction of Lam Tin Interchange | Resident of Yau Lai Estate Bik Lai House | Noise | The complainant complained the construction noise generated at Lam Tin Interchange. | Y | | Closed |
| 25 | 26 th January 2017 | Not Specified / Construction Works near Eastern Harbour Crossing tunnel portal | 黃國健議員及何啟明議員 | Noise | LC members referred complaints about the noise generated by the construction works near the EHC tunnel portal. They mentioned that the noise generated by the construction works had greatly affected the daily life of nearby residents, especially occupants of Block 5 of Yau Lai Estate and those who lived at the upper floors. | Y | <p>After investigation, it was found out that necessary rock breaking works by hydraulic or pneumatic breakers was conducted during excavation for tunnel adit at Lam Tin Interchange. Noise nuisance from the works area is considered due to the high noise level emission during use of hydraulic or pneumatic breakers.</p> <p>The Contractor had implemented environmental mitigation measures in accordance with the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual.</p> <p>The Contractor has taken the initiative to implement additional noise mitigation measures in order to further minimize noise nuisance to the nearby sensitive receivers, including the followings:</p> <ul style="list-style-type: none"> ➤ Provision and installation of additional temporary noise barrier during rock breaking works for construction of Lam Tin Interchange; ➤ Commencement time of daily construction works for construction of Lam Tin Interchange has been postponed from 7am to 8am each day. | Closed |
| 26 | 27 th January 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Yau Lai Estate Bik Lai House | Noise | The complainant complained the construction noise generated at Lam Tin Interchange at 7am in the morning. (EPD Ref No. K15/RE/00002945-17) | Y | According to information provided by the Contractor, powered Mechanical Equipment being operated on site during the time of complaint include breaker, dump truck, backhoes, drilling rig, mobile crane and small bulldozer. They were operated on and off with some idling time. It is considered that noise nuisance during the time of complaint was mainly due to high noise level emission during the use of breaker for rock breaking. | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|--------------------------------|---|---|-------------|---|-------------------------------------|--|-------------|
| 27 | 9 th February 2017 | Not Specified / construction of Lam Tin Interchange | Resident of Yat Lai House, Yau Lai Estate | Noise | The complainant complained about the noise nuisance during the construction works of Lam Tin Interchange at 8:10am. (EPD Reference No.: K15/RE/00003855-17) | Y | In addition to the the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual, the Contractor has implemented the following additional noise mitigation measures since late including: <ul style="list-style-type: none"> ● Provision and installation of additional temporary noise barrier during rock breaking works for construction of Lam Tin Interchange; ● Sound absorptive materials with 50mm thickness were hanged on rock mountain wall as well as temporary noise barrier containers; and ● Adoption of alternative rock breaking method such as partial rock breaking by rock splitter. | Closed |
| 28 | 13 th February 2017 | Not Specified / construction of Lam Tin Interchange | Resident of Yat Lai House, Yau Lai Estate | Noise | The complainant complained about the noise nuisance during the construction works of Lam tin Interchange. | Y | In addition, the Contractor has taken the initiative to explore measures to further reduce construction noise nuisance such as: <ul style="list-style-type: none"> ● Installation of cantilever barrier on top of the containers; ● Installation of tuned mass dampers on breaker head; and ● Use of acoustic mat cover and a retractable noise barrier where feasible. <p>According to the regular noise monitoring no Limit Level Exceedance was recorded at Noise Monitoring Station CM1, Station CM2 and Station CM3 from 2 – 15 February 2017. With the implementation of environmental mitigation measures by Contractors on site, it is considered that no adverse air quality and noise impact was brought to the nearby sensitive receivers by the works of this Project.</p> | Closed |
| 29 | 23 rd February 2017 | 18 Feb 2017 / Slope Works at Lei Yue Mun Road | Anonymous | Air Quality | The complainant complained about the dust generated by the slope works opposite to Lam Tin Ambulance Depot on 18 February 2017 afternoon. He mentioned that the dust greatly affected | N | The major source of construction dust nuisance was construction of a temporary storage area. As per investigation, the Contractor has provided environmental mitigation measures to prevent dust generation for the slope works. Water spray was prepared and provided next to the works for dust suppression during the use of handheld breaker. | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|--------------------------------|---|---|---------------------|---|-------------------------------------|--|-------------|
| | | | | | the pedestrian. | | | |
| 30 | 23 rd February 2017 | Not Specified / BMCPC Footpath | Sai Kung District Council Member Mr. Chan Kai Wai | (Safety) | Mr. Chan complained that some of the excavated materials fell from the dump trucks on the BMCPC footpath affecting the safety of pedestrian and hikers. | N | The major source of construction dust nuisance was formation of temporary site haul road. As per investigation, the following environmental mitigation measures are implemented by the Contractor: <ul style="list-style-type: none"> ➤ Water truck was provided for dust suppression at least 8 times per day along the footpath within our site boundary; ➤ Wheel washing were provided for all dump trucks once loaded; ➤ All the dump trucks were covered properly with a mechanical cover once loaded. ➤ The dump trucks were loaded in a specific area (off the footpath) near the formation works area. | Closed |
| 31 | 2 nd March 2017 | Not Specified / Construction Works near BMCPC Footpath | A resident of Ocean Shores | Air Quality | The complainant complained about the dust generated by the construction works near the existing BMCPC footpath | N | <ul style="list-style-type: none"> ➤ The dump trucks were loaded in a specific area (off the footpath) near the formation works area. | Closed |
| 32 | 8 th March 2017 | 7 Mar 2017 / Slope works near Sin Fat Road Tennis Court | Public | Air Quality & Noise | The complainant complained the dust and noise generated by the slope works near Sin Fat Road Tennis Court | Y | The major source of construction dust and noise nuisance was shotcreting of slope surface, and drilling for soil nail. As per investigation, the following environmental mitigation measures are implemented by the Contractor: <ul style="list-style-type: none"> ➤ Tarpaulin sheets were provided along the slope adjacent to the tennis court during shotcreting; ➤ After the complaint was received, the dust screen for tennis court has been enhanced immediately with additional tarpaulin along the fencing of tennis court; ➤ Additional acoustic sheets were also provided to minimize construction noise nuisance to users of the tennis courts; ➤ At the location of shotcreting / drilling of slope works, additional tarpaulin sheet was placed at source to minimize dust generation due to the works | Closed |
| 33 | 10 th March 2017 | 4 Mar 2017 / Slope works near Sin Fat Road Tennis Court | Anonymous | Air Quality | The complainant complained the dust generated by the slope works near Sin Fat Road Tennis Court. | N | <ul style="list-style-type: none"> ➤ Tarpaulin sheets were provided along the slope adjacent to the tennis court during shotcreting; ➤ After the complaint was received, the dust screen for tennis court has been enhanced immediately with additional tarpaulin along the fencing of tennis court; ➤ Additional acoustic sheets were also provided to minimize construction noise nuisance to users of the tennis courts; ➤ At the location of shotcreting / drilling of slope works, additional tarpaulin sheet was placed at source to minimize dust generation due to the works | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|-----------------------------|--|---------------|-----------------------------------|--|-------------------------------------|--|-------------|
| 34 | 13 th March 2017 | 27 Feb – 12 Mar 2017 / Barging point in front of Ocean Shore | Public | Noise | The complainant complained about noise from the loading / unloading activities at the barging point in front of Ocean Shore for material delivery to the LT-TKO Tunnel work site during 3:00 am and 4:00am over the past 2 weeks. | Y | <p>According to information provided by the Contractors, no works, including any loading / unloading works, was carried out during the restricted hours at site area near Ocean Shores in early March 2017. The complaint is concluded to be non-Project related.</p> <p>The Engineer and the Environmental Team have reminded the contractor(s) not to carry out any works, especially loading/unloading activities near the Ocean Shores during restricted hours to minimize noise nuisance to the nearby residents.</p> | Closed |
| 35 | 21 st March 2017 | Not Specified / Construction Works near Cha Kwo Ling Village | 茶果嶺鄉民聯誼會書記鍾先生 | Water & Waste/Chemical Management | The complainant stated that villagers concerned about the waste water produced by car washing in construction site will flow into the sea/ existing drainage system directly and requested the contractors to improve the situation. | N | <p>In accordance with the information provided by the Contractor of the Project, vehicle wheel washing near Cha Kwo Ling Village was carried out site access of Portion I and Portion WAI. At Portion I, a ‘WetSep’ wastewater treatment system was installed to treat wastewater from vehicle washing. For Portion WAI, surface runoff collection system is also installed near the site access. Also, concrete sand bag bunds are provided near seafront of Portion WAI to prevent wastewater flowing into the sea.</p> <p>Despite, the Contractor was reminded to fully implement the relevant water quality mitigation measures according to the EM&A Manual on site. The Contractor was also recommended to provide training for all workers again to increase awareness of their environmental responsibilities and properly collect and treat all wastewater generated due to construction works.</p> | Closed |
| 36 | 25 th March 2017 | Not Specified / Construction Works of TKO Portal | Public | Air Quality | The complainant complaint about the construction dust impact due to marine works and construction of tunnel of this Project. | N | <p>The major source of construction dust and noise nuisance was site formation works for TKO Portal and marine works for construction of temporary barging facilities</p> <p>As per investigation, the following environmental mitigation measures are implemented by the Contractor:</p> <ul style="list-style-type: none"> ➤ Provision of frequent watering including watering of eight times a day on active work area, exposed area and paved haul roads; ➤ Installation of automatic sprinklers for water spray to minimize dust generation; | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|----------------------------|--|--|---------------------|--|-------------------------------------|---|-------------|
| | | | | | | | <ul style="list-style-type: none"> ➤ Shotcreting or hydroseeding to surface of TKO Portal site formation; ➤ Provision of wheel washing to vehicles out of site; ➤ Covering of dusty slope surface by impervious material such tarpaulin sheets. <p>During the weekly site inspections by the Environmental Team (ET), no deficiencies about exhaust gas or black smoke generation was observed from the Powered Mechanical Equipment (PME) on site of construction of TKO Portal. Air quality impact due to exhaust gas or black smoke emission from PME is considered insignificant from the Project.</p> | |
| 37 | 6 th April 2017 | 1 Apr 2017 / Slope works near Sin Fat Road Tennis Court | Public | Air Quality | The complainant complained the smell and dust generated by the slope works near Sin Fat Road Tennis Court on 1 April 2017. He suspected that the shotcrete may contain toxic substances and may affect the health. | N | See Investigation / Mitigation Action for Complaint No. 32 and 33. | Closed |
| 38 | 4 th May 2017 | Not Specified / Construction site near Nga Lai House, Yau Lai Estate | Kwun Tong District Council Member Mr. Lai Shu Ho | Noise | The complainant complained about construction noise nuisance near Nga Lai House, Yau Lai Estate and lack of noise mitigation measures during construction works. | Y | According to information provided by the Contractor, necessary rock breaking work was carried out in May 2017 by excavator-mounted breakers and drill rig at Portion IVC, which is in close vicinity of the complainant. Also, 2 nos. of excavator / drill rig were operated in May 2017 for excavation and drilling and rock hill. Noise nuisance concerned by the complainant is considered due to the high noise level emission during use of these Powered Mechanical Equipment (PME). | Closed |
| 39 | 8 th May 2017 | Not Specified / Construction site near Yau Lai Estate | Kwun Tong District Council Member Mr. Lai Shu Ho | Air Quality & Noise | The complainant complained about construction noise nuisance and air pollution generated by this Project. | Y | The Contractors had implemented environmental mitigation measures on site according to the EM&A Manual to reduce air quality impact and noise nuisance to the vicinity. Weekly Environmental Site Inspection has been on-going in May 2017. Recommendations was made on site by the Engineer and the ET to increase the effectiveness of the noise mitigation measures. | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|---------------------------|---|-------------|-------------|--|-------------------------------------|---|-------------|
| | | | | | | | According to the regular air quality monitoring conducted at Air Quality Monitoring Stations AM3, no Action or Limit Level Exceedance was recorded from 4, 10 and 16 May 2017. Similarly, no Limit Level Exceedance was recorded in May 2017 at Noise Monitoring Station CM1 and CM2. With the implementation of environmental mitigation measures by Contractors on site, it is considered that no adverse air quality and noise impact was brought to the nearby sensitive receivers by the works of this Project. | |
| 40 | 9 th May 2017 | Not Specified / Construction of Road P2 near Ocean Shores | Public | Noise | The complainant complained about noise and environmental nuisance resulting from the piling works. | Y | <p>Major construction activities near Ocean Shores in early May included sheetpiling works and pre-boring works for construction of Road P2. Powered Mechanical Equipments (PME) operated included drilling rigs and piling rigs (vibration hammer), which are considered to be the source of noise nuisance resulting from piling work.</p> <p>The Contractor had implemented environmental mitigation measures in accordance with the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual and the approved Noise Mitigation Plan. Movable temporary noise barrier is erected on ground in vicinity of the piling areas to reduce noise emission during piling works. Acoustic material are also hanged on the piling rigs to shield noise from the Powered Mechanical Equipment (PME) to nearby noise sensitive receivers.</p> <p>According to the regular noise monitoring conducted at Noise Monitoring Stations CM6(A) and CM7(A), no Limit Level Exceedance was recorded from 1- 14 May 2017. With the implementation of environmental mitigation measures by Contractors on site, it is considered that no adverse noise impact was brought to the nearby sensitive receivers by the works of this Project.</p> | Closed |
| 41 | 10 th May 2017 | Not Specified / Construction of Road P2 near Ocean Shores | Public | Noise | The complainant complained about noise nuisance from the use of the generators until midnight. | Y | <p>During evening time, two generators were operated between 7pm - 11pm for site office use only. No generators were used until midnight according to the Contractor.</p> <p>Additional temporary noise barrier is installed by the Contractor to screen noise due to use of generators during evening time</p> | Closed |
| 42 | 10 th May 2017 | Not Specified / Slope works near Sin Fat Road Tennis | Public | Air Quality | The complainant complained about the generation of construction dust | N | See Investigation / Mitigation Action for Complaint No. 32 and 33. | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|---------------------------|--|--|--------|---|-------------------------------------|---|-------------|
| | | Court | | | from this Project | | | |
| 43 | 15 th May 2017 | Not Specified / Construction site at Lei Yue Mun Road | Kwun Tong District Council Member Mr. Lai Shu Ho | Noise | The complainant complained about construction noise nuisance during construction works at work site at Lei Yue Mun Road. | Y | See Investigation / Mitigation Action for Complaint No. 38 and 39. | Closed |
| 44 | 16 th May 2017 | Not Specified / Construction site near Nga Lai House, Yau Lai Estate | Public | Noise | The complainant complained about construction noise nuisance during construction works at work site near Nga Lai House, Yau Lai Estate from 8 am to 7 pm. | Y | See Investigation / Mitigation Action for Complaint No. 38 and 39. | Closed |
| 45 | 17 th May 2017 | 3 rd May 2017 / Marine Works Area in TKO Side | Public | Noise | The complainant complained about the noisy ongoing construction works on a public holiday. | Y | No marine works was carried out under Contract No. NE/2015/01 on public holidays on 30 April, 1 May and 3 May 2017. While marine construction works was carried out on public holiday under Contract No. NE/2015/02 on 3 May 2017 between 9am to 5pm. One derrick barge was operated for the marine works during this period.no violation of CNP (No. GW-RE0317-17) conditions is observed during the time of complaint. The Engineer and the Environmental Team have reminded the contractor(s) to minimize construction works during public holidays or restricted hours to minimize noise nuisance to the nearby residents. | Closed |
| 46 | 25 th May 2017 | Not Specified / Construction site near Tin Hau Temple | 茶果嶺鄉民聯誼會主席羅悅屏 | Noise | The complainant complaint about the noisy rock breaking works near Tin Hau Temple and poor efficiency of vehicle wheel washing on site. | Y | According to information provided by the Contractor of the Project, excavation and rock breaking by 1 no. of excavator/excavator-mounted breaker was carried out intermittently during daytime of the time of complaint near Tin Hau Temple. The tip of the breaker is wrapped with acoustic blanket and followed by erection of noise barrier. A wheel washing bay had been installed at the site entrance on Cha Kwo Ling Road to construction of Lam Tin Interchange. A 'WetSep' wastewater treatment system was installed to treat wastewater from vehicle washing washing. | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|---------------------------|---|---|-------------|--|-------------------------------------|---|-------------|
| | | | | | | | The Contractor was reminded to fully implement on site the relevant noise and water quality mitigation measures according to the EM&A Manual and the approved Noise Mitigation Plan. | |
| 47 | 27 th May 2017 | Not Specified / Construction site at Lei Yue Mun Road | Public | Noise | The complainant complained about construction noise nuisance during construction works at work site at Lei Yue Mun Road. | Y | See Investigation / Mitigation Action for Complaint No. 38 and 39. | Closed |
| 48 | 1 st June 2017 | Not Specified / Construction site near Yung Lai House, Yau Lai Estate | Public | Noise | The complainant complained about construction dust and noise nuisance during construction works at work site near Yung Lai House, Yau Lai Estate (EPD Reference No.: K15/RE/00016902-17) | Y | <p>According to the information provided by the Contractor, the major construction activities performed in June and mid-July included excavation and drilling in Portion IVC near Lei Yue Mun Road, excavation and rock breaking at Lam Tin Interchange and rock breaking next to Yau Tong Site Office.</p> <p>The Contractor had implemented environmental mitigation measures in accordance with the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual as below:</p> <p><u>Air Quality:</u></p> <ul style="list-style-type: none"> • Water spraying was provided during breaking works at Portion IVC, slope G of Lam Tin Interchange and works area near Yau Tong Site Office to minimize dust generation due to the works. <p><u>Noise:</u></p> <ul style="list-style-type: none"> • Operating PMEs at Portion IVC, slope G of Lam Tin Interchange and works area near Yau Tong Site Office were on and off with idling time. • Excavator-mounted breakers were mounted with acoustic sheets. • Noise barriers were erected during the breaking works at Portion IV, slope G of Lam Tin Interchange and works area near Yau Tong Site Office to minimize construction noise nuisance. <p>With the implementation of environmental mitigation measures by Contractors on site, it is considered that air quality and noise nuisance by the works has been brought to a minimum level.</p> | Closed |
| 49 | 7 th June 2017 | 7 th June 2017 / Construction site near Sin Fat Road | Correspondent of Sin Fat Road Tennis Courts | Air Quality | The complainant complained about construction dust nuisance near the | N | In accordance with the information provided by the Contractor of the Project, the major construction activities at the location of complaints were shotcreting of slope surface and drilling for soil nail near Sin Fat Road Tennis Court. | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|----------------------------|--|---|---------------------|---|-------------------------------------|--|-------------|
| | | Tennis Courts | | | tennis courts. | | <p>The Contractor immediately stopped the shotcreting works adjacent to the tennis courts upon the complaint, and re-schedule the works such that the shotcreting works near the tennis court are performed only when the tennis courts are not in use. The Contractor also cleared the dust brought by the construction in the tennis courts on the same day of the complaint.</p> <p>the Contractor was reminded to fully implement the relevant air quality mitigation measures according to the EM&A Manual on site.</p> | |
| 50 | 8 th June 2017 | 30 th May 2017 / marine works area inside the cofferdam installed under the Project | Sai Kung District Council Member Mr. Chan Kai Wai | Noise | The complainant complained about marine construction work being carried out on 30 May 2017 (a public holiday) within the reclamation area near Ocean Shore under this Project (EPD Reference No.: N08/RE/019540-17) | Y | According to information provided by the Contractor and confirmation by the Engineer, no marine construction activities were conducted on public holiday on 30th May 2017 within the cofferdams installed in the reclamation area under this Project. The complaint on 30th May 2017 therefore considered to be non-Project related. | Closed |
| 51 | 15 th June 2017 | Not Specified / Construction site near Nga Lai House, Yau Lai Estate | Public | Air Quality & Noise | The complainant complained about construction dust and noise nuisance during construction works at work site near Nga Lai House, Yau Lai Estate. (EPD Reference No.: K15/RE/00018656-17) | Y | See Investigation / Mitigation Action for Complaint No. 48. | Closed |
| 52 | 21 st June 2017 | Not Specified / Construction site near Yau Lai Estate | Public | Noise | The complainant complained about construction noise nuisance from work site near Yau Lai | Y | See Investigation / Mitigation Action for Complaint No. 48. | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|----------------------------|--|---|----------------------------|---|-------------------------------------|---|-------------|
| | | | | | Estate. | | | |
| 53 | 24 th June 2017 | 24 th June 2017 / land-based works area near Ocean Shores | Resident of Ocean Shores | Noise | The complainant complained about construction noise nuisance from land-based works area near Ocean Shores | Y | <p>According to the information provided by the Contractor, the major construction activities during the time of complaint includes breaking of hard material.</p> <p>Upon received of the complaint, the Contractor has taken the initiative to minimize construction noise nuisance by erecting temporary noise barrier during rock breaking works.</p> <p>Nonetheless, the Contractor was recommended to implement and strictly follow the noise mitigation measures as recommended in the EM&A Manual and Noise Mitigation Plan in order to reduce construction noise impact on site.</p> | Closed |
| 54 | 26 th June 2017 | 26 th June 2017 / marine works area near Ocean Shores | Public | Waste/ Chemical Management | The complainant complained about oil spill on sea near marine works site near Ocean Shores | N | <p>According to the information provided by the Contractor, marine works were conducted on 26 June 2017, including lifting operation for the concrete block from water gate to derrick barge. 3 derrick barges and 3 sampan were in operation for the marine works.</p> <p>According to records of the Contractor, no report of oil spill from the derrick barges was received from the site foremen. Oil spillage was not found in the afternoon on 26 June 2017. Therefore, the complaint is considered to be non-Project related.</p> | Closed |
| 55 | 27 th June 2017 | 25 th June 2017/ marine works area near Ocean Shores | Sai Kung District Council Member Mr. Chan Kai Wai | Noise | The complainant complained about marine construction work being carried out on public holidays within the marine works area near Ocean Shore under this Project | Y | <p>Minor marine construction activities was conducted on public holiday 25th June 2017 within the reclamation area under this Project. Removal of damaged parts of steel cofferdam, which are damaged under adverse weather conditions in June 2017.</p> <p>The Engineer and the Environmental Team reminded the Contractor(s) not to conduct any works near Ocean Shores during public holidays (including Sundays) to avoid noise nuisance to the nearby residents. Also, no use of PME will be allowed for general holidays (including Sundays) at marine works area under this Contract according to the latest CNP granted to the Contractor.</p> | Closed |
| 56 | 6 th July 2017 | Not Specified / Construction site near Yau Lai Site Office | Resident of Yat Lai House, Yau Lai Estate | Noise | The complainant complained about construction noise nuisance from work site near Yau Tong Site Office. | Y | See Investigation / Mitigation Action for Complaint No. 48. | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|-----------------------------|---|---|---------------|--|-------------------------------------|--|-------------|
| 57 | 14 th July 2017 | Not Specified / Construction sites near Cha Kwo Ling Road | Kwun Tong District Council Member Mr. Mok Kin Shing | Air Quality | The complainant complained about construction dust nuisance due to works and vehicles on Cha Kwo Ling Road | N | <p>The Contractor had implemented the following to reduce dust nuisance caused by construction vehicles on Cha Kwo Ling Road:</p> <ul style="list-style-type: none"> ➤ Mobilize water trucks to perform water spraying along Cha Kwo Ling Road to suppress dust generation due to movement of vehicles ➤ Dispatch workers to clear dust near vehicle exits from the construction site on Cha Kwo Ling Road. ➤ Performing frequent water spraying by water trucks on Cha Kwo Ling Road; ➤ Frequent clearance of dust near site exits on Cha Kwo Ling Road; ➤ Provision of wheel washing for site vehicles at paved site exits to reduce vehicle tracking of soil on Cha Kwo Ling Road; <p>Despite, the Contractor was reminded to fully implement the relevant air quality mitigation measures according to the EM&A Manual on site, including:</p> <ul style="list-style-type: none"> ➤ Maintenance of wheel washing machines on a regular basis to ensure sand and silt settled out in wash-water; ➤ Reminding all site vehicles to perform wheel washing before leaving the site; and ➤ To ensure materials on construction trucks are covered by impervious materials before leaving the site to prevent fugitive emission. | Closed |
| 58 | 18 th July 2017 | Not Specified / Construction sites near Yau Lai Estate | Yau Lai Estate Property Services Management Office | Noise | The complainant complained about construction noise nuisance from work site near Yau Lai Estate. | Y | See Investigation / Mitigation Action for Complaint No. 48. | Closed |
| 59 | 2 nd August 2017 | 2 nd August 2017 / construction site under this Project in Tseung Kwan | Drainage Services Department | Water Quality | Muddy flow was noted in Tseung Kwan O DSD desilting compound. Muddy discharge | N | According to information provided by the Contractor, no discharge of muddy water was reported and wastewater treatment system were functioned properly on the day of event. No muddy effluent discharge was recorded from the weekly site inspection reports in July. The site effluent was appeared visually acceptable in | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|-----------------------------|---|-------------|-----------------------------|--|-------------------------------------|--|-------------|
| | | O | | | <p>should be flow down along the western one / two cell(s) of the DSD box culvert underneath the desilting compound.</p> <p>The complainant suspected that TKO-LT Tunnel project should be the major construction site discharging into the cell(s).</p> | | <p>reference to the results of daily visual checking by the Contractor and the weekly site inspection conducted on 3rd August, 2017.</p> <p>The Contractor has taken initiatives to ensure the quality of the wastewater discharge from the construction site as followed:</p> <ul style="list-style-type: none"> ➤ Temporary drainage system were developed on site and number of sub-drains were distributed within the site area to divert wastewater and allow longer settling time for surface runoff prior to further treatment before discharging ➤ Daily visual checking was conducted to check the physical appearance of treated effluent and to ensure proper performance of the wastewater treatment system. ➤ Manholes were adequately covered and temporarily sealed to prevent silt, construction materials or debris being washed into the drainage system ➤ Apart from visual checking, inspection of effluent was provided by the Contractor on rainy days to make sure the quality of treated wastewater discharge is in compliance of the discharge license requirements. <p>It is considered that the wastewater generated from the construction activities of the Project was collected and treated properly before discharging to the designated discharge point on 2nd August, 2017. As the same discharge point is shared by other box culverts, it is considered that the source of silty discharge at location of complaint was runoff or effluent collected from other upstream sources such as that collected by drainage systems in Tseung Kwan O town centre and other construction sites in vicinity.</p> | |
| 60 | 2 nd August 2017 | Not Specified / construction site at Lei Yun Mun Road | Anonymous | Landscape and Visual Impact | The complainant complained the long tree branches and weeds and request proper trimming. | N | <p>According to the information provided by the Contractor, clearance of weeds adjacent to Lam Tin Ambulance Depot and pruning of overgrown trees within the Site area have been undertaken by the Contractor.</p> <p>Upon received of the complaint, the Contractor has taken the initiative to remove weeds adjacent to Lam Tin Ambulance Depot.</p> | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|------------------------------|---|---|-----------------------------|---|-------------------------------------|---|-------------|
| | | | | | | | In addition, the Contractor has performed pruning of excess branches of trees on Lei Yue Mun Road and established fencing of tree protection zones for existing trees. | |
| 61 | 11 th August 2017 | Not Specified / construction site in Green Cross-hatched Black Area near Ocean Shores | Sai Kung District Council Member Mr. Chan Kai Wai | Landscape and Visual Impact | The complainant complained the poor health and condition of trees and lack of tree protection facility. | N | Based on the information gather in the investigation, it is considered that retained trees adjacent to the construction area of Portion IV are carefully managed and properly fenced off within the tree protection zone. No heavy vehicles or equipment stationed in the vicinity of retained tree and tree protection zone are observed free from storage and dumping. Tree Survey and Tree Assessment Reports are conducted by qualified Arborist (ISA Certified Arborist) to monitor the performance of the retained trees throughout the construction period. Advance tree survey works were done and consent was granted from the Engineer for the removal of defective trees. | Closed |
| 62 | 11 th August 2017 | 9 th August 2017 / construction site in Green Cross-hatched Black Area near Ocean Shores | Sai Kung District Council Member Mr. Chan Kai Wai | Landscape and Visual Impact | The complainant complained the poor health and condition of trees; and that they were felled. | N | | |
| 63 | 11 th August 2017 | Not Specified / construction site near Ocean Shores near the BMCPC footpath | Sai Kung District Council Member Mr. Chan Kai Wai | Landscape and Visual Impact | The complainant complained that trees within the Project Site were felled. | N | | |
| 64 | 14 th August 2017 | Not Specified / construction site near Ocean Shores near the BMCPC footpath | Sai Kung District Council Member Mr. Chan Kai Wai | Landscape and Visual Impact | The complainant complained that trees within the Project Site were felled. | N | | |
| 65 | 15 th August 2017 | 15 th August 2017 / marine works site at TKO side | Sai Kung District Council Member Mr. Chan Kai Wai | Water Quality | Muddy discharge from the marine works site (near the Type 2 cofferdam) at TKO side occurred in the morning. | N | It is considered that the muddy discharge was caused by the overflowing of coarse material within the steel tank and the sediment being disturbed by the cofferdam during the reinstatement of the position of steel tank. The Contractor did not stop the works immediately and which contributed to the large spreading area of sediment. The Contractor did not provide proper deployment of the silt curtain system to stop the muddy discharge | Closed |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|--------------------------------|---|-------------|-----------------------------|---|-------------------------------------|--|-------------|
| | | | | | | | <p>generated from the abovementioned work to the surrounding water. The Contractor is advised to implement the following measures to avoid/ minimize the generation of muddy discharge from marine works:</p> <ol style="list-style-type: none"> 1. Marine works should be stopped immediately when the silt curtain system is found malfunctioned or when sediment dispersion is observed. 2. Deterioration of cofferdam or silt curtain, as the mitigation measures to water quality, should be repaired immediately or at a reasonable time. 3. Cofferdams should be designed and installed properly in order to withstand any conceivable adverse weather conditions and precautions measure should be taken in advance particularly during typhoon season. 4. Materials with high silt content should be avoided to use as filling materials in the steel tanks for cofferdams. They should be replaced with materials with minimal silt content, such as pebbles, rocks and etc. to reduce pollution to the marine environment when spill over. 5. The steel tanks filled with finer aggregate materials should be securely covered or locked in the tank, so that no materials will be spilled over the sea. 6. Silt curtain should be deployed properly before commencement of works. 7. Regular inspection should be performed to examine the integrity of the cofferdam and performance of silt curtains. | |
| 66 | 17 th August 2017 | Not Specified / construction site at Lei Yun Mun Road | Anonymous | Landscape and Visual Impact | The complainant complained the long tree branches and lack of tree protection facilities on site. | N | See Investigation / Mitigation Action for Complaint No. 60. | Closed |
| 67 | 1 st September 2017 | Not Specified / near Eastern Harbour Crossing | Anonymous | Landscape and Visual Impact | The complainant complained poor tree health and lack of tree protection facilities on site. | N | Under Investigation | On-going |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|--------------------------------|---|-------------|-----------------------------|---|-------------------------------------|--|-------------|
| 68 | 4 th September 2017 | Not Specified / Construction site near Sin Fat Road Tennis Courts | Public | Air Quality | The complainant complained the construction dust and odour nuisance | N | <p>According to the information provided by the Contractor, the major construction activities during the time of complaint included excavation, rock breaking.</p> <p>The Contractor had implemented environmental mitigation measures in accordance with the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual as below:</p> <ul style="list-style-type: none"> ➤ Breaking works were provided with water spraying to reduce fugitive emission; ➤ Tarpaulin sheets were provided along Sin Fat Road Tennis Court; ➤ Frequent water spraying on unpaved area and haul roads at Lam Tin Interchange; ➤ Wheel washing facility at exits of Lam Tin Interchange to prevent mud trailing of vehicles and dust generation. <p>According to the regular air quality monitoring, no Action or Limit Level Exceedance was recorded at Air Quality Monitoring Station AM2 and AM3 in September 2017. With the implementation of environmental mitigation measures by Contractors on site, it is considered that no adverse air quality impact was brought to the nearby sensitive receivers by the works of this Project.</p> <p>The following recommendations were given by the ET to further enhance effectiveness of the mitigation measures:</p> <ul style="list-style-type: none"> ➤ To provide a hard-surfaced road between any cleaning facility and the public road ➤ To treat exposed earth by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen or other suitable surface stabilizer within six months after the last construction activity within the site; ➤ Where practicable, to provide sheltered area on the top and three sides for stockpiles of dusty materials, or perform frequent water spraying so as to maintain the entire surface wet. | On-going |
| 69 | 5 th September 2017 | Not Specified / near Eastern Harbour Crossing | Anonymous | Landscape and Visual Impact | The complainant complained poor tree health and lack of tree protection facilities on site. | N | Under Investigation | On-going |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|---------------------------------|---|-----------------------------|-----------------------------|---|-------------------------------------|--|-------------|
| | 19 th September 2017 | Not Specified / near Eastern Harbour Crossing | Anonymous | Landscape and Visual Impact | The complainant complained poor tree health and lack of tree protection facilities on site. | N | | |
| 70 | 9 th September 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Ping Tin Estate | Noise | The complainant complained daytime noise nuisance that commenced early in the morning | Y | <p>According to the information provided by the Contractor, the major construction activities at the location of complaint recorded included excavation, rock breaking and drilling during September 2017.</p> <p>Operated PME during the time of complaints are consistent with the proposed quantities in the latest Construction Noise Assessment.</p> <p>The Contractor had implemented environmental mitigation measures in accordance with the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual as below:</p> <ul style="list-style-type: none"> ➤ Erected noise barriers with acoustic mats facing Ping Tin Estate and along breaking works at Portion IVc; ➤ Powered mechanical equipment (PME) for rock breaking were equipped with TMD and SilentMat. | On-going |
| | 22 nd September 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Ping Tin Estate | Noise | The complainant complained daytime construction noise nuisance. | Y | <p>According to the regular noise monitoring, no Limit Level Exceedance was recorded at Noise Monitoring Station CM1, Station CM2 and Station CM3 in September 2017. With the implementation of environmental mitigation measures by Contractors on site, it is considered that no adverse noise impact was brought to the nearby sensitive receivers by the works of this Project.</p> <p>The following recommendations were given by the ET to further enhance effectiveness of the mitigation measures:</p> <ul style="list-style-type: none"> ➤ Frequent checking and repair the gaps or broken tarpaulin sheets and acoustic sheets; ➤ To adopt Cantilever noise barriers at Lam Tin Interchange to screen noise effectively; ➤ To continue to properly implement noise mitigation measures as recommended in the Environmental Monitoring & Audit Manual and approved Noise Mitigation Plan; ➤ To continue to strictly follow the requirements in the approved Noise Mitigation Plan; and ➤ To reschedule operation time and reduce operation duration of each PME. | |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|---------------------------------|---|---|---------------------|---|-------------------------------------|--|-------------|
| 71 | 11 th September 2017 | 3 rd September 2017 / Construction of Lam Tin Interchange | Anonymous | Noise | The complainant complained the noise nuisance during night time blasting works at the Lam Tin Interchange | Y | <p>The Contractor had taken the initiative to implement environmental mitigation measures specified to blasting as below:</p> <ul style="list-style-type: none"> ➤ Installed steel-type blasting door mounted with sound absorptive lining to absorb noise from blasting in the tunnel; ➤ Ensured blasting doors were fully closed when blasting works were undertaken ➤ Erected noise barriers with TMD and SilentMAT adjacent to blasting door facing Yau Lai Estate ➤ Placed acoustic materials on slopes adjacent to blasting door <p>With the implementation of environmental mitigation measures by Contractors on site, it is considered that blasting noise impact to the nearby sensitive receivers has been brought to a minimum.</p> | On-going |
| | 21 st September 2017 | 19 th September 2017 / Construction of Lam Tin Interchange | Anonymous | Noise | The complainant complained the noise nuisance during night time blasting works at the Lam Tin Interchange | Y | | |
| 72 | 11 th September 2017 | Not Specified / Construction of Tseung Kwan O Portal | Resident of Ocean Shores | Air Quality | The complainant complained the construction dust nuisance | N | <p>According to the information provided by the Contractor, the major construction activities at the location of complaint recorded included breaking works and shotcreting works from 0830 hrs to 1800 hrs during early September 2017.</p> <p>The Contractor had implemented environmental mitigation measures in accordance with the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual as below:</p> <ul style="list-style-type: none"> ➤ Water spraying on unpaved or exposed area for dust suppression; ➤ Breaking of rocks was provided with water spraying to reduce fugitive emission; ➤ Automatic water sprinklers were provided and in operation; ➤ Manual water spraying was provided to haul roads to reduce dust generation due to movement of construction vehicles; ➤ Tarpaulin sheets were erected along the access road to reduce dust nuisance to pedestrians. | Closed |
| | 12 th September 2017 | Not Specified / Construction of Tseung Kwan O Portal | Resident of Ocean Shores | Air Quality | The complainant complained the construction dust nuisance | N | | |
| 73 | 12 th September 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Nga Lai House, Yau Lai Estate | Air Quality / Noise | The complainant complained the construction dust and noise nuisance from works | Y | See Investigation / Mitigation Action for Complaint No. 68 and 70. | On-going |
| 74 | 15 th September | Not Specified / Construction | Resident of Laguna City | Noise | The complainant complained the | Y | See Investigation / Mitigation Action for Complaint No. 70. | On-going |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|---------------------------------|---|--|--------|--|-------------------------------------|---|-------------|
| | 2017 | of Lam Tin Interchange | | | construction noise nuisance from works | | | |
| 75 | 18 th September 2017 | Not Specified / Construction of Lam Tin Interchange | Kwun Tong District Council Member Mr. Lai Shu Ho | Noise | The complainant complained the noise nuisance during night time blasting works at the LamTin Interchange | Y | See Investigation / Mitigation Action for Complaint No. 71. | On-going |
| 76 | 21 st September 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Yung Lai House, Yau Lai Estate | Noise | The complainant complained daytime noise nuisance that commenced early in the morning | Y | See Investigation / Mitigation Action for Complaint No. 70. | On-going |
| 77 | 26 th September 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Cheuk Lai House, Yau Lai Estate | Noise | The complainant complained about the night time construction noise nuisance | Y | See Investigation / Mitigation Action for Complaint No. 70. | On-going |
| 78 | 26 th September 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Laguna City | Noise | The complainant complained the blasting noise nuisance during works at the Lam Tin Interchange | Y | See Investigation / Mitigation Action for Complaint No. 71. | On-going |
| 79 | 27 th September 2017 | 17 th , 20 th , 23 rd September 2017 / Construction of Lam Tin Interchange | Public | Noise | The complainant complained about the construction noise nuisance due to road works near Lam Tin Interchange. | Y | See Investigation / Mitigation Action for Complaint No. 70. | On-going |
| 80 | 28 th September 2017 | Not Specified / Construction of Lam Tin Interchange | Property Management Office of Laguna City | Noise | The complainant complained the noise nuisance during night time blasting works at the LamTin Interchange | Y | See Investigation / Mitigation Action for Complaint No. 71. | On-going |
| 81 | 3 rd October 2017 | 30 th September 2017 / Construction | Sai Kung District Council | Noise | The complainant complained that construction works | Y | Under Investigation | On-going |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|-------------------------------|---|-------------------------|-----------------------------|--|-------------------------------------|--|-------------|
| | | of Road P2 | Member Mr. Chan Kai Wai | | starts too early between 8-9 am on 30 September 2017 (Saturday). | | | |
| 82 | 3 rd October 2017 | Not Specified / CRE Site Office | Anonymous | Landscape and Visual Impact | The complainant complained the long tree branches and weeds and lack of tree protection facilities. | N | Under Investigation | On-going |
| 83 | 6 th October 2017 | 6 th October 2017 / Construction of TKO Portal | Public | Waste Management | The complainant complained that construction waste was disposed on slope near O King Road. | N | Under Investigation | On-going |
| 84 | 17 th October 2017 | 17 th October 2017 / Marine Works Area for Road P2 | Public | Water Quality | The complainant concerns marine water pollution in Tseung Kwan O on 17 Oct 2017, which might due to construction activities of this Project. | N | <p>Based on the information gathered in the investigation, it is considered that muddy water recorded by the complainant was not caused by the construction activities (land-based and marine-based) carried out during the time of complaint. Also, wastewater generated from the construction activities of the Project was collected and treated properly before discharging as the site effluent was appeared visually acceptable and the wastewater treatment systems were preformed properly.</p> <p>As the location of the muddy water was appeared adjoining the Tseung Kwan O DSD Desilting Compound, a high volume of upstream discharge collected from rain events (3-4 am of 17 October 2017) is a possible cause of muddy water.</p> <p>Based on the above observations and findings, this complaint is considered to be non-Project related.</p> | Closed |
| 85 | 18 th October 2017 | Not Specified / Construction of Lam Tin Interchange | Public | Noise | The complainant complained about the noise nuisance due to construction of Lam Tin Interchange | Y | Under Investigation | On-going |

| Complaint No. | Received Date | Date/Location of Complaint | Complainant | Nature | Details of Complaint | Noise Action Level Exceedance (Y/N) | Investigation/ Mitigation Action | File Closed |
|---------------|-------------------------------|---|---|-------------|---|-------------------------------------|----------------------------------|-------------|
| 86 | 25 th October 2017 | 24 th October 2017 / Construction of Lam Tin Interchange | Public | Air & Noise | The complainant complained about the noise nuisance due to blasting works at nighttime and request water spraying on breakers. | Y | Under Investigation | On-going |
| 87 | 26 th October 2017 | 23 th October 2017 / Construction of marine works outside Ocean Shores | Public | Noise | The complainant complaint about noise nuisance which may due to construction of marine work outside Ocean Shores at nighttime. | Y | Under Investigation | On-going |
| 88 | 27 th October 2017 | Not Specified / Construction of Lam Tin Interchange | Resident of Bik Lai House, Yau Lai Estate | Noise | The complainant complained about noise nuisance as it is observed that no acoustic materials are provided to breaker. She also complained about the noise nuisance due to blasting works at nights. | Y | Under Investigation | On-going |

Note

(1): The complaints were received in this reporting period and yet to be included in the previous Monthly EM&A Reports.

(2): Previous case received on 26 Sep 2017 on construction noise nuisance fin Tseung Kwan O is confirmed to be Enquiry on the Project instead of a documented complaint.

Cumulative Complaint Log since commencement of Project

| Reporting Month | Number of Complaints in Reporting Month | Number of Summons in Reporting Month | Number of Prosecutions in Reporting Month |
|------------------------|--|---|--|
| November 2016 | 0 | 0 | 0 |
| December 2016 | 11 | 0 | 0 |
| January 2017 | 15 | 0 | 0 |
| February 2017 | 4 | 0 | 0 |
| March 2017 | 6 | 0 | 0 |
| April 2017 | 1 | 0 | 0 |
| May 2017 | 10 | 0 | 0 |
| June 2017 | 8 | 0 | 0 |
| July 2017 | 3 | 0 | 0 |
| August 2017 | 8 | 0 | 0 |
| September 2017 | 14 | 0 | 0 |
| October 2017 | 8 | 0 | 0 |
| Total | 88 | 0 | 0 |

Cumulative Log for Notifications of Summons

| Contract No. | Log Ref. | Date/Location | Subject | Status | Total no. Received in this reporting month | Total no. Received since project commencement |
|---------------------|-----------------|----------------------|----------------|---------------|---|--|
| NE/2015/01 | -- | -- | -- | -- | -- | -- |
| NE/2015/02 | -- | -- | -- | -- | -- | -- |
| NE/2015/03 | -- | -- | -- | -- | -- | -- |

Cumulative Log for Successful Prosecutions

| Contract No. | Log Ref. | Date/Location | Subject | Status | Total no. Received in this reporting month | Total no. Received since project commencement |
|---------------------|-----------------|----------------------|----------------|---------------|---|--|
| NE/2015/01 | -- | -- | -- | -- | -- | -- |
| NE/2015/02 | -- | -- | -- | -- | -- | -- |
| NE/2015/03 | -- | -- | -- | -- | -- | -- |

**APPENDIX P
WASTE GENERATION IN THE
REPORTING MONTH**

Monthly Summary Waste Flow Table for 2017



| Month | Actual Quantities of Inert C&D Materials Generated Monthly | | | | | | Actual Quantities of C&D Wastes Generated Monthly | | | | |
|-----------|--|--|---------------------------|-----------------------------|---|--------------------------|---|--|---|-------------------|--------------------------------|
| | a.Total Quantity Generated (see Note 8) | b. Hard Rock and Large Broken Concrete | c. Reused in the Contract | d. Reused in Other Projects | e. Disposed as Public Fill (see Note 10) | f. Imported Fill | g. Metals (see Note 5) | h. Paper / Cardboard Packaging (see Note 5) | i. Plastics (see Note 3) (see Note 5) | j. Chemical Waste | k. Others, e.g. general refuse |
| | (in '000m ³) | (in '000m ³) | (in '000m ³) | (in '000m ³) | (in '000m ³) | (in '000m ³) | (in '000kg) | (in '000kg) | (in '000kg) | (in '000kg) | (in '000m ³) |
| January | 40.484 | 1.350 | 22.688 | 5.063 | 12.733 | 0.000 | 0.000 | 0.257 | 0.000 | 0.000 | 0.292 |
| February | 23.357 | 5.159 | 12.911 | 3.874 | 6.572 | 0.000 | 0.000 | 0.000 | 0.000 | 1.000 | 0.488 |
| March | 20.078 | 2.885 | 6.359 | 11.713 | 2.006 | 0.000 | 0.000 | 0.120 | 0.000 | 0.000 | 0.284 |
| April | 13.516 | 0.070 | 4.862 | 7.751 | 0.903 | 0.000 | 0.000 | 0.151 | 0.000 | 0.000 | 0.396 |
| May | 49.156 | 0.380 | 12.420 | 36.168 | 0.568 | 0.000 | 0.000 | 0.000 | 0.000 | 0.000 | 0.189 |
| June | 37.960 | 2.949 | 17.914 | 19.409 | 0.637 | 0.000 | 0.000 | 0.114 | 0.000 | 0.000 | 0.138 |
| Sub-total | 184.551 | 12.793 | 77.154 | 83.978 | 23.419 | 0.000 | 0.000 | 0.642 | 0.000 | 1.000 | 1.787 |
| July | 33.640 | 2.302 | 4.851 | 28.223 | 0.566 | 0.000 | 0.000 | 0.160 | 0.000 | 0.000 | 0.166 |
| August | 65.934 | 2.483 | 6.054 | 52.830 | 7.050 | 0.000 | 0.000 | 0.146 | 0.000 | 0.000 | 0.082 |
| September | 64.150 | 12.654 | 10.483 | 52.113 | 1.554 | 0.000 | 0.000 | 0.233 | 0.000 | 0.000 | 0.082 |
| October | 47.354 | 18.954 | 9.708 | 33.995 | 3.651 | 0.000 | 0.000 | 0.000 | 0.000 | 0.000 | 0.044 |
| November | | | | | | | | | | | |
| December | | | | | | | | | | | |
| Total | 395.629 | 49.186 | 108.250 | 251.139 | 36.240 | 0.000 | 0.000 | 1.181 | 0.000 | 1.000 | 2.161 |

Total inert C&D waste generated = c+d+e

Total inert C&D waste recycled = c+d

$$\% \text{ of recycled inert C\&D waste} = \frac{\text{Total C\&D waste recycled}}{\text{Total C\&D waste generated}}$$

Monthly Summary Waste Flow Table for 2017 Year

| Month | Actual Quantities of Inert C&D Materials Generated Monthly | | | | | | Actual Quantities of C&D Wastes Generated Monthly | | | | |
|------------------|--|-------------------------------------|--------------------------|--------------------------|--------------------------|--------------------------|---|-----------------------------|-----------------------|----------------|----------------------------|
| | Total Quantity Generated | Hard Rock and Large Borken Concrete | Reused in the Contract | Reused in other Projects | Disposal as Public Fill | Imported Fill | Metals | Paper / Cardboard Packaging | Plastics (See note 3) | Chemical Waste | Other, e.g. general refuse |
| | [in '000m ³] | [in '000m ³] | [in '000m ³] | [in '000m ³] | [in '000m ³] | [in '000m ³] | [in '000kg] | [in '000kg] | [in '000kg] | [in '000kg] | [in '000m ³] |
| Jan | 1.07155 | 0.00000 | 0.05040 | 0.00000 | 1.02115 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.02306 |
| Feb | 1.05393 | 0.00000 | 0.00000 | 0.00000 | 1.05393 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.02132 |
| Mar | 0.03860 | 0.00000 | 0.00000 | 0.00000 | 0.03860 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.03012 |
| Apr | 0.96584 | 0.00000 | 0.94400 | 0.00000 | 0.02184 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.18326 |
| May | 0.80922 | 0.00000 | 0.00000 | 0.75824 | 0.05099 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.11508 |
| June | 6.52844 | 0.00000 | 0.39000 | 0.17665 | 5.96179 | 0.00000 | 9.82000 | 0.00000 | 0.00000 | 0.00000 | 0.03430 |
| SUB-TOTAL | 10.46758 | 0.00000 | 1.38440 | 0.93489 | 8.14829 | 0.00000 | 9.82000 | 0.00000 | 0.00000 | 0.00000 | 0.40714 |
| Jul | 5.97521 | 0.00000 | 0.00000 | 0.00000 | 5.97521 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.03072 |
| Aug | 4.00624 | 0.00000 | 0.02641 | 0.00000 | 3.97983 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.00000 | 0.17294 |
| Sep | 7.31145 | 0.00000 | 0.00000 | 0.00000 | 7.31145 | 0.00000 | 11.86000 | 0.00000 | 0.00000 | 0.00000 | 0.12258 |
| Oct | 2.14193 | 0.00000 | 0.00000 | 0.00000 | 1.85075 | 0.29118 | 28.23000 | 0.00000 | 0.00000 | 0.00000 | 0.03040 |
| Nov | | | | | | | | | | | |
| Dec | | | | | | | | | | | |
| TOTAL | 29.90241 | 0.00000 | 1.41081 | 0.93489 | 27.26553 | 0.29118 | 49.91000 | 0.00000 | 0.00000 | 0.00000 | 0.76378 |

Note: Conversion to 1000m³ for general refuse is weight in 1000kg multiply by 0.002

Conversion to 1000m³ for Inert C&D is weight in 1000kg multiply by 0.0005

Plastics refer to plastic bottles / containers, plastic sheets / foam from packaging material

Name of Department : CEDD

Contract No. : NE/2015/03

Monthly Summary Waste Flow Table for 2017 (year)

| Month | Actual Quantities of Inert C&D Materials Generated Monthly | | | | | | Actual Quantities of C&D Wastes Generated Monthly | | | | |
|-----------|--|-----------------------------------|---------------------------|---------------------------|---------------------------|---------------------------|---|----------------------------|-----------------------|-----------------|-----------------------------|
| | Total Quantity Generated | Hard Rock & Large Broken Concrete | Reused in the Contract | Reused in other Projects | Disposed as Public Fill | Imported Fill | Metals | Paper/ cardboard packaging | Plastics (see Note 3) | Chemicals Waste | Others, e.g. general refuse |
| | (in '000 m ³) | (in '000 m ³) | (in '000 m ³) | (in '000 m ³) | (in '000 m ³) | (in '000 m ³) | (in '000 kg) | (in '000 kg) | (in '000 kg) | (in '000 kg) | (in '000 m ³) |
| Jan | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| Feb | 0.001982 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0.001982 |
| Mar | 0.00146 | 0 | 0 | 0 | 0.00146 | 0 | 0 | 0 | 0 | 0 | 0 |
| Apr | 0.008668 | 0 | 0 | 0 | 0.0075 | 0 | 0 | 0 | 0 | 0 | 0.001168 |
| May | 0.01052 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0.01052 |
| June | 0.03652 | 0 | 0 | 0 | 0 | 0.03056 | 0 | 0 | 0 | 0 | 0.00596 |
| Sub-total | 0.046428 | 0 | 0 | 0 | 0.00896 | 0 | 0 | 0 | 0 | 0 | 0.01963 |
| July | 0.01207 | 0 | 0 | 0 | 0.01207 | 0 | 0 | 0 | 0 | 0 | 0 |
| Aug | 0.1074 | 0 | 0 | 0 | 0.1074 | 0 | 0 | 0 | 0 | 0 | 0 |
| Sept | 0.008115 | 0 | 0 | 0 | 0.008115 | 0 | 0 | 0 | 0 | 0 | 0 |
| Oct | 0.4018 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0.00946 |
| Nov | | | | | | | | | | | |
| Dec | | | | | | | | | | | |
| Total | 0.281895 | 0 | 0 | 0 | 0.163355 | 0.03056 | 0 | 0 | 0 | 0 | 0.04872 |

- Notes:
- (1) The performance targets are given in PS Clause 6.14.
 - (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
 - (4) The *Contractor* shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the *works*, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the *works* is equal to or exceeding 50,000 m³.

**APPENDIX Q
TENTATIVE CONSTRUCTION
PROGRAMME**

High Level 3 Months Look Ahead Programme

| Activities | Nov-17 | Dec-17 | Jan-18 |
|--|--------|--------|--------|
| Lam Tin Interchange | | | |
| EHC2 U-Trough | | | |
| Site Formation - Area 1G1 & 1G2 &5 | | | |
| Site Formation - Area 2 | | | |
| Site Formation - Area 3 | | | |
| Site Formation - Area 4 | | | |
| Pipe Pile Wall - Area 2A | | | |
| Main Tunnel | | | |
| MT Excavation | | | |
| TKO Interchange | | | |
| Haul Road Construction, Site Formation & Slope Works | | | |
| Temporary Cut Slope For BMCPC | | | |
| Temporary Barging Facilities & Temporary Works | | | |
| Steel Platform for Bridge Construction | | | |

| Activity ID | Activity Name | Calendar | Original Duration | Remaining Duration | Start | Finish | Total Float | Activity % Complete | Variance - BL1 | TRA | 2017 | | | | 2018 | | |
|--|--|----------|-------------------|--------------------|-------------|-----------|-------------|---------------------|----------------|-----|------|-----|-----|-----|------|--|--|
| | | | | | | | | | | | Oct | Nov | Dec | Jan | Feb | | |
| S11432 | Prepare and Submit DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 3) | P2-Cal.A | 21 | 21 | 24-Nov-17 | 14-Dec-17 | -19 | 0% | | | | | | | | | |
| S11434 | Review and Discuss DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 3) | P2-Cal.A | 21 | 21 | 15-Dec-17 | 04-Jan-18 | -19 | 0% | | | | | | | | | |
| S11436 | Resubmit DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 3) | P2-Cal.A | 14 | 14 | 05-Jan-18 | 18-Jan-18 | -19 | 0% | | | | | | | | | |
| S11438 | Review and comment by GEO | P2-Cal.A | 14 | 14 | 19-Jan-18 | 01-Feb-18 | -19 | 0% | | | | | | | | | |
| E&M Design | | P2-Cal.A | 292 | 78 | 24-Jan-17 A | 05-Jan-18 | 43 | | | | | | | | | | |
| Statutory Approval for E&M Works | | P2-Cal.A | 0 | 0 | 10-Dec-17 | 10-Dec-17 | 69 | | | | | | | | | | |
| S11570-11 | FSD Approval for Underpass GBP | P2-Cal.A | 0 | 0 | | 10-Dec-17 | 69 | 0% | | | | | | | | | |
| S11570-12 | FSD Approval for Plant room GBP | P2-Cal.A | 0 | 0 | | 10-Dec-17 | 69 | 0% | | | | | | | | | |
| Detail Design for E&M Works (Tunnel and associated) | | P2-Cal.A | 292 | 78 | 24-Jan-17 A | 05-Jan-18 | 43 | | | | | | | | | | |
| MVAC Detail Design | | P2-Cal.A | 31 | 31 | 13-Oct-17 A | 19-Nov-17 | 50 | | | | | | | | | | |
| Plantroom | | P2-Cal.A | 16 | 23 | 13-Oct-17 A | 11-Nov-17 | 58 | | | | | | | | | | |
| S11576 | 1st review by EMSD/HyD | P2-Cal.A | 8 | 8 | 13-Oct-17 A | 27-Oct-17 | 58 | 0% | 16 | | | | | | | | |
| S11577 | Formal Submission to Supervisor | P2-Cal.A | 8 | 8 | 28-Oct-17 | 04-Nov-17 | 58 | 0% | 0 | | | | | | | | |
| S11578 | Accept detail design by the Supervisor | P2-Cal.A | 7 | 7 | 05-Nov-17 | 11-Nov-17 | 58 | 0% | 0 | | | | | | | | |
| Underpass | | P2-Cal.A | 31 | 31 | 20-Oct-17 | 19-Nov-17 | 50 | | | | | | | | | | |
| S11625 | 1st review by EMSD/HyD | P2-Cal.A | 15 | 15 | 20-Oct-17 | 03-Nov-17 | 50 | 0% | 0 | | | | | | | | |
| S11630 | Formal Submission to Supervisor | P2-Cal.A | 9 | 9 | 04-Nov-17 | 12-Nov-17 | 50 | 0% | 0 | | | | | | | | |
| S11640 | Accept detail design by the Supervisor | P2-Cal.A | 7 | 7 | 13-Nov-17 | 19-Nov-17 | 50 | 0% | 0 | | | | | | | | |
| FS Detail Design | | P2-Cal.A | 22 | 22 | 20-Oct-17 | 10-Nov-17 | 59 | | | | | | | | | | |
| Underpass | | P2-Cal.A | 22 | 22 | 20-Oct-17 | 10-Nov-17 | 59 | | | | | | | | | | |
| S11650 | 1st review by FSD/EMSD | P2-Cal.A | 15 | 15 | 20-Oct-17 | 03-Nov-17 | 59 | 0% | 0 | | | | | | | | |
| S11651 | Accept detail design by the Supervisor | P2-Cal.A | 7 | 7 | 04-Nov-17 | 10-Nov-17 | 59 | 0% | 0 | | | | | | | | |
| Plantroom | | P2-Cal.A | 22 | 22 | 20-Oct-17 | 10-Nov-17 | 59 | | | | | | | | | | |
| S11652-09 | 1st review by FSD/EMSD | P2-Cal.A | 15 | 15 | 20-Oct-17 | 03-Nov-17 | 59 | 0% | 0 | | | | | | | | |
| S11652-10 | Accept detail design by the Supervisor | P2-Cal.A | 7 | 7 | 04-Nov-17 | 10-Nov-17 | 59 | 0% | 0 | | | | | | | | |
| Plumbing and Drainage Detail Design | | P2-Cal.A | 284 | 70 | 10-Feb-17 A | 28-Dec-17 | 51 | | | | | | | | | | |
| Underpass | | P2-Cal.A | 284 | 70 | 10-Feb-17 A | 28-Dec-17 | 31 | | | | | | | | | | |
| S11653 | Prepare and submit detail design for PD services | P2-Cal.A | 21 | 21 | 10-Feb-17 A | 09-Nov-17 | 31 | 0% | -214 | | | | | | | | |
| S11654 | 1st review of the submission by the Supervisor | P2-Cal.A | 7 | 7 | 10-Nov-17 | 16-Nov-17 | 31 | 0% | 0 | | | | | | | | |
| S11655 | Resubmit detail design for PD services | P2-Cal.A | 7 | 7 | 17-Nov-17 | 23-Nov-17 | 31 | 0% | 0 | | | | | | | | |
| S11656 | 2nd review from Supervisor | P2-Cal.A | 7 | 7 | 24-Nov-17 | 30-Nov-17 | 31 | 0% | 0 | | | | | | | | |
| S11657 | 1st review by HyD | P2-Cal.A | 14 | 14 | 01-Dec-17 | 14-Dec-17 | 31 | 0% | 0 | | | | | | | | |
| S11658 | Formal Submission to Supervisor | P2-Cal.A | 7 | 7 | 15-Dec-17 | 21-Dec-17 | 31 | 0% | 0 | | | | | | | | |
| S11659 | Accept detail design by the Supervisor | P2-Cal.A | 7 | 7 | 22-Dec-17 | 28-Dec-17 | 31 | 0% | 0 | | | | | | | | |
| Plantroom | | P2-Cal.A | 34 | 39 | 20-Oct-17 A | 27-Nov-17 | 82 | | 3 | | | | | | | | |
| S11660-08-2 | 6th review from Supervisor | P2-Cal.A | 8 | 8 | 20-Oct-17 A | 27-Oct-17 | 82 | 0% | 34 | | | | | | | | |
| S11660-09 | 1st review by HyD/EMSD | P2-Cal.A | 15 | 15 | 28-Oct-17 | 11-Nov-17 | 82 | 0% | 0 | | | | | | | | |
| S11660-10 | Formal Submission to Supervisor | P2-Cal.A | 8 | 8 | 12-Nov-17 | 19-Nov-17 | 82 | 0% | 0 | | | | | | | | |
| S11660-11 | Accept detail design by the Supervisor | P2-Cal.A | 8 | 8 | 20-Nov-17 | 27-Nov-17 | 82 | 0% | 0 | | | | | | | | |
| Electrical Detail Design | | P2-Cal.A | 292 | 78 | 24-Jan-17 A | 05-Jan-18 | 22 | | | | | | | | | | |
| Underpass Lighting | | P2-Cal.A | 61 | 20 | 26-Jul-17 A | 08-Nov-17 | 41 | | 0 | | | | | | | | |
| S11660-16 | 1st review by EMSD/HyD | P2-Cal.A | 15 | 6 | 26-Jul-17 A | 25-Oct-17 | 41 | 60% | -32 | | | | | | | | |
| S11660-17 | Formal Submission to Supervisor | P2-Cal.A | 7 | 7 | 26-Oct-17 | 01-Nov-17 | 41 | 0% | 0 | | | | | | | | |
| S11660-18 | Accept detail design by the Supervisor | P2-Cal.A | 7 | 7 | 02-Nov-17 | 08-Nov-17 | 41 | 0% | 0 | | | | | | | | |
| External Road Lighting | | P2-Cal.A | 22 | 29 | 08-Sep-17 A | 17-Nov-17 | 42 | | 0 | | | | | | | | |
| S11660-23 | 1st review by EMSD/CLP/ HyD | P2-Cal.A | 14 | 14 | 08-Sep-17 A | 02-Nov-17 | 42 | 0% | 7 | | | | | | | | |
| S11660-24 | Formal Submission to Supervisor | P2-Cal.A | 7 | 7 | 03-Nov-17 | 09-Nov-17 | 42 | 0% | 0 | | | | | | | | |

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Oct-17)

3 Months Rolling Programme
 (20 October 2017)
 Page: 2 of 11

| Date | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 20-Oct-17 | | | |

| Activity ID | Activity Name | Calendar | Original Duration | Remaining Duration | Start | Finish | Total Float | Activity % Complete | Variance - BL1 Finish Date | TRA | 2017 | | | | | 2018 | |
|---|---|----------|-------------------|--------------------|-------------|-----------|-------------|---------------------|----------------------------|-----|------|-----|-----|-----|-----|------|--|
| | | | | | | | | | | | Oct | Nov | Dec | Jan | Feb | | |
| S11660-25 | Accept detail design by the Supervisor | P2-Cal.A | 8 | 8 | 10-Nov-17 | 17-Nov-17 | 42 | 0% | 0 | | | | | | | | |
| Plantroom | | P2-Cal.A | 292 | 78 | 24-Jan-17 A | 05-Jan-18 | 22 | | 0 | | | | | | | | |
| S11661 | Prepare and submit detail design for EL services | P2-Cal.A | 21 | 21 | 24-Jan-17 A | 09-Nov-17 | 22 | 0% | -214 | | | | | | | | |
| S11663 | 1st review of the submission by the Supervisor | P2-Cal.A | 8 | 8 | 10-Nov-17 | 17-Nov-17 | 22 | 0% | 0 | | | | | | | | |
| S11664 | Resubmit detail design for EL services | P2-Cal.A | 8 | 8 | 18-Nov-17 | 25-Nov-17 | 22 | 0% | 0 | | | | | | | | |
| S11665 | 2nd review from Supervisor | P2-Cal.A | 10 | 10 | 26-Nov-17 | 05-Dec-17 | 22 | 0% | 0 | | | | | | | | |
| S11666 | 1st review by EMSD/HyD | P2-Cal.A | 15 | 15 | 06-Dec-17 | 20-Dec-17 | 22 | 0% | 0 | | | | | | | | |
| S11667 | Formal Submission to Supervisor | P2-Cal.A | 8 | 8 | 21-Dec-17 | 28-Dec-17 | 22 | 0% | 0 | | | | | | | | |
| S11668 | Accept detail design by the Supervisor | P2-Cal.A | 8 | 8 | 29-Dec-17 | 05-Jan-18 | 22 | 0% | 0 | | | | | | | | |
| ELV And SCADA Detail Design | | P2-Cal.A | 31 | 41 | 04-Oct-17 A | 29-Nov-17 | 50 | | 0 | | | | | | | | |
| Underpass | | P2-Cal.A | 31 | 41 | 04-Oct-17 A | 29-Nov-17 | 50 | | 0 | | | | | | | | |
| S11669-04 | 2nd review from Supervisor | P2-Cal.A | 10 | 10 | 04-Oct-17 A | 29-Oct-17 | 50 | 0% | 30 | | | | | | | | |
| S11669-05 | 1st review by HyD | P2-Cal.A | 15 | 15 | 30-Oct-17 | 13-Nov-17 | 50 | 0% | 0 | | | | | | | | |
| S11669-06 | Formal Submission to Supervisor | P2-Cal.A | 8 | 8 | 14-Nov-17 | 21-Nov-17 | 50 | 0% | 0 | | | | | | | | |
| S11669-07 | Accept detail design by the Supervisor | P2-Cal.A | 8 | 8 | 22-Nov-17 | 29-Nov-17 | 50 | 0% | 0 | | | | | | | | |
| Plantroom | | P2-Cal.A | 31 | 41 | 04-Oct-17 A | 29-Nov-17 | 50 | | 0 | | | | | | | | |
| S11670-04 | 2nd review from JV/Supervisor | P2-Cal.A | 10 | 10 | 04-Oct-17 A | 29-Oct-17 | 50 | 0% | 30 | | | | | | | | |
| S11670-05 | 1st review by HyD | P2-Cal.A | 15 | 15 | 30-Oct-17 | 13-Nov-17 | 50 | 0% | 0 | | | | | | | | |
| S11670-06 | Formal Submission to Supervisor | P2-Cal.A | 8 | 8 | 14-Nov-17 | 21-Nov-17 | 50 | 0% | 0 | | | | | | | | |
| S11670-07 | Accept detail design by the Supervisor | P2-Cal.A | 8 | 8 | 22-Nov-17 | 29-Nov-17 | 50 | 0% | 0 | | | | | | | | |
| Design of Architectural Finishes for Internal Walls of U-Trough Structures | | P2-Cal.A | 77 | 77 | 20-Oct-17 | 04-Jan-18 | 232 | | 0 | | | | | | | | |
| S11675 | Prepare and Submit Design of Architectural Finishes for Internal Walls of U-Trough Structures (VE and PC Panel) | P2-Cal.A | 21 | 21 | 20-Oct-17 | 09-Nov-17 | 232 | 0% | 0 | | | | | | | | |
| S11680 | Review and Discuss Design of Architectural Finishes for Internal Walls of U-Trough Structures (VE and PC Panel) | P2-Cal.A | 21 | 21 | 10-Nov-17 | 30-Nov-17 | 232 | 0% | 0 | | | | | | | | |
| S11700 | Resubmit Design of Architectural Finishes for Internal Walls of U-Trough Structures (VE and PC Panel) | P2-Cal.A | 14 | 14 | 01-Dec-17 | 14-Dec-17 | 232 | 0% | 0 | | | | | | | | |
| S11720 | Review and Accept Design of Architectural Finishes for Internal Walls of U-Trough Structures (VE and PC Panel) | P2-Cal.A | 21 | 21 | 15-Dec-17 | 04-Jan-18 | 232 | 0% | 0 | | | | | | | | |
| Irrigation System | | P2-Cal.A | 132 | 61 | 21-Jun-17 A | 19-Dec-17 | 0 | | 0 | | | | | | | | |
| S11781 | Comment from Supervisor | P2-Cal.A | 21 | 21 | 21-Jun-17 A | 09-Nov-17 | 0 | 0% | -71 | | | | | | | | |
| S11782 | Reviewed by WSD | P2-Cal.A | 5 | 5 | 10-Nov-17 | 14-Nov-17 | 0 | 0% | 0 | | | | | | | | |
| S11783 | Formal Submission to Supervisor | P2-Cal.A | 14 | 14 | 15-Nov-17 | 28-Nov-17 | 0 | 0% | 0 | | | | | | | | |
| S11800 | Review and Accept Submission for Waterpoints and associated elements | P2-Cal.A | 21 | 21 | 29-Nov-17 | 19-Dec-17 | 0 | 0% | 0 | | | | | | | | |
| Contractor Cost Saving Design | | P2-Cal.A | 98 | 98 | 20-Oct-17 | 25-Jan-18 | 459 | | 0 | | | | | | | | |
| AIP Submission for CSD of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355) | | P2-Cal.A | 56 | 56 | 20-Oct-17 | 14-Dec-17 | 459 | | 0 | | | | | | | | |
| S11940 | Resubmit AIP Submission for CSD of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355) | P2-Cal.A | 28 | 28 | 20-Oct-17 | 16-Nov-17 | 459 | 0% | 0 | | | | | | | | |
| S11950 | Review and Accept AIP Submission for CSD of Reclaimed Section by HyD (S200 CH674 - CH755, S300 CH326-CH355) | P2-Cal.A | 28 | 28 | 17-Nov-17 | 14-Dec-17 | 459 | 0% | 0 | | | | | | | | |
| S11960 | Review and Accept AIP Submission for CSD of Reclaimed Section by CEDD (S200 CH674 - CH755, S300 CH326-CH355) | P2-Cal.A | 21 | 21 | 17-Nov-17 | 07-Dec-17 | 466 | 0% | 0 | | | | | | | | |
| DDA Submission for CSD of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355) | | P2-Cal.A | 42 | 42 | 15-Dec-17 | 25-Jan-18 | 459 | | 0 | | | | | | | | |
| S11962 | Prepare and Submit DDA Submission for CSD of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355) | P2-Cal.A | 21 | 21 | 15-Dec-17 | 04-Jan-18 | 459 | 0% | 0 | | | | | | | | |
| S11964 | Review and Discuss DDA Submission for CSD of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355) | P2-Cal.A | 21 | 21 | 05-Jan-18 | 25-Jan-18 | 459 | 0% | 0 | | | | | | | | |
| Major Temporary Works Design | | P2-Cal.A | 154 | 111 | 27-Sep-17 A | 07-Feb-18 | 47 | | 0 | | | | | | | | |
| Reinstatement Works of Temporary Steel Cofferdam (Type 2A, 2B, 2C & 2D) | | P2-Cal.A | 12 | 12 | 20-Oct-17 | 31-Oct-17 | -284 | | 0 | | | | | | | | |
| S12134-24 | Review and Accept Design of Temporary Steel Cofferdam Type 2A,2B,2C & 2D(CE057) | P2-Cal.A | 12 | 12 | 20-Oct-17 | 31-Oct-17 | -284 | 0% | 0 | | | | | | | | |
| Reinstatement Works of Double Water Gate | | P2-Cal.A | 21 | 12 | 14-Oct-17 A | 31-Oct-17 | -284 | | 0 | | | | | | | | |
| S12134-44 | Review and Accept Design of Double Water Gate System (CE057) | P2-Cal.A | 21 | 12 | 14-Oct-17 A | 31-Oct-17 | -284 | 42.86% | 0 | | | | | | | | |
| ELS Design for U-Trough A & B (P2 CH318 - CH363) Existing Tong Yin Street | | P2-Cal.A | 76 | 49 | 27-Sep-17 A | 07-Dec-17 | -62 | | 0 | | | | | | | | |
| S12480 | Review and Discuss ELS Design for U-Trough A & B (P2 CH318 - CH363) | P2-Cal.A | 21 | 21 | 27-Sep-17 A | 09-Nov-17 | -62 | 0% | -27 | | | | | | | | |
| S12500 | Resubmit ELS Design for U-Trough A & B (P2 CH318 - CH363) + CE No.12 IW (T8 1day) | P2-Cal.A | 7 | 7 | 10-Nov-17 | 16-Nov-17 | -62 | 0% | 0 | | | | | | | | |
| S12520 | Accept ELS Design for U-Trough A & B (P2 CH318 - CH363) + CE No.12 IW (T8 1day) | P2-Cal.A | 21 | 21 | 17-Nov-17 | 07-Dec-17 | -62 | 0% | 0 | | | | | | | | |

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Oct-17)

3 Months Rolling Programme
 (20 October 2017)
 Page: 3 of 11

| Date | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 20-Oct-17 | | | |

| Activity ID | Activity Name | Calendar | Original Duration | Remaining Duration | Start | Finish | Total Float | Activity % Complete | Variance - BL1 Finish Date | TRA | 2017 | | | | | 2018 | | |
|--|---|----------|-------------------|--------------------|-------------|-----------|-------------|---------------------|----------------------------|-----|------|------|-----|-----|-----|------|------|--|
| | | | | | | | | | | | Oct | Nov | Dec | Jan | Feb | | | |
| ELS Design for Road P2 Underpass (Non-Plant Room Section) P2 CH105-CH318 | | | | | | | | | | | | Oct | | | | | 2018 | |
| S12760 | Accept ELS Design for Road P2 Underpass (CH105-318) | P2-Cal.A | 21 | 21 | 07-Oct-17 A | 09-Nov-17 | 60 | 0% | 47 | | | | | | | | | |
| ELS Design for Road P2 Underpass (Plant Rooms) P2 CH105-CH318 | | | | | | | | | | | | Nov | | | | | 2018 | |
| S17900 | Pre. and Sub. ELS Design for Road P2 Underpass (Incl.Stom.W Pt Rm, Sump Pit Rm & Fixed Foam Tk Rm) | P2-Cal.A | 18 | 18 | 10-Nov-17 | 27-Nov-17 | 60 | 0% | 0 | | | | | | | | | |
| S17920 | Rev. and Disc. ELS Design for Road P2 Underpass (Incl.Stom.W Pt Rm, Sump Pit Rm & Fixed Foam Tk Rm) | P2-Cal.A | 21 | 21 | 28-Nov-17 | 18-Dec-17 | 60 | 0% | 0 | | | | | | | | | |
| S17940 | Resubmit ELS Design for Road P2 Underpass (Incl.Stom.W Pt Rm, Sump Pit Rm & Fixed Foam Tk Rm) | P2-Cal.A | 38 | 38 | 19-Dec-17 | 25-Jan-18 | 60 | 0% | 0 | | | | | | | | | |
| Design of concrete block (Due to insufficient material and stockpile area) (4 Layer Concrete Block) | | | | | | | | | | | | Dec | | | | | 2018 | |
| S12935 | Accept Design of concrete block (Due to insufficient material and stockpile area) | P2-Cal.A | 21 | 14 | 12-Oct-17 A | 02-Nov-17 | -38 | 33.33% | -36 | | | | | | | | | |
| Temporary Jetty Design | | | | | | | | | | | | Jan | | | | | 2018 | |
| S13020 | Prepare and Submit Temporary Jetty Design | P2-Cal.A | 18 | 18 | 31-Dec-17 | 17-Jan-18 | -174 | 0% | 0 | | | | | | | | | |
| S13040 | Review and Discuss Temporary Jetty Design | P2-Cal.A | 21 | 21 | 18-Jan-18 | 07-Feb-18 | -174 | 0% | 0 | | | | | | | | | |
| Design of Marine Survey Tower | | | | | | | | | | | | Feb | | | | | 2018 | |
| S13100 | Prepare and Submit Marine Survey Tower | P2-Cal.A | 18 | 18 | 20-Oct-17 | 06-Nov-17 | -270 | 0% | 0 | | | | | | | | | |
| S13120 | Review and Discuss Marine Survey Tower | P2-Cal.A | 21 | 21 | 07-Nov-17 | 27-Nov-17 | -270 | 0% | 0 | | | | | | | | | |
| S13140 | Resubmit Temporary Marine Survey Tower | P2-Cal.A | 14 | 14 | 28-Nov-17 | 11-Dec-17 | -270 | 0% | 0 | | | | | | | | | |
| S13160 | Accept Temporary Marine Survey Tower | P2-Cal.A | 21 | 21 | 12-Dec-17 | 01-Jan-18 | -270 | 0% | 0 | | | | | | | | | |
| Major Construction Works Method Statement | | | | | | | | | | | | 2018 | | | | | 2018 | |
| Construction of Seawall Foundation for Road P2 | | | | | | | | | | | | 2018 | | | | | 2018 | |
| S13260 | Prepare and Submit Method Statement for Construction of Seawall Foundation for Road P2 | P2-Cal.A | 18 | 18 | 11-Nov-17 | 28-Nov-17 | -229 | 0% | 0 | | | | | | | | | |
| S13280 | Review and Discuss Method Statement for Construction of Seawall Foundation for Road P2 | P2-Cal.A | 21 | 21 | 29-Nov-17 | 19-Dec-17 | -229 | 0% | 0 | | | | | | | | | |
| S13300 | Resubmit Method Statement for Construction of Seawall Foundation for Road P2 | P2-Cal.A | 7 | 7 | 20-Dec-17 | 26-Dec-17 | -229 | 0% | 0 | | | | | | | | | |
| S13320 | Accept Method Statement for Construction of Seawall Foundation for Road P2 | P2-Cal.A | 21 | 21 | 27-Dec-17 | 16-Jan-18 | -229 | 0% | 0 | | | | | | | | | |
| Reclamation Filling | | | | | | | | | | | | 2018 | | | | | 2018 | |
| S13340 | Prepare and Submit Method Statement for Reclamation Filling | P2-Cal.A | 18 | 18 | 20-Oct-17 | 06-Nov-17 | -260 | 0% | 0 | | | | | | | | | |
| S13360 | Review and Discuss Method Statement for Reclamation Filling | P2-Cal.A | 21 | 21 | 07-Nov-17 | 27-Nov-17 | -260 | 0% | 0 | | | | | | | | | |
| S13380 | Resubmit Method Statement for Reclamation Filling | P2-Cal.A | 7 | 7 | 28-Nov-17 | 04-Dec-17 | -260 | 0% | 0 | | | | | | | | | |
| S13400 | Accept Method Statement for Reclamation Filling | P2-Cal.A | 21 | 21 | 05-Dec-17 | 25-Dec-17 | -260 | 0% | 0 | | | | | | | | | |
| Demolishing/ Removing Existing Amour | | | | | | | | | | | | 2018 | | | | | 2018 | |
| S13620 | Resubmit Method Statement for Demolishing/ Removing Existing Amour | P2-Cal.A | 7 | 7 | 20-Oct-17 | 26-Oct-17 | -282 | 0% | 0 | | | | | | | | | |
| S13640 | Accept Method Statement for Demolishing/ Removing Existing Amour | P2-Cal.A | 7 | 7 | 27-Oct-17 | 02-Nov-17 | -282 | 0% | 0 | | | | | | | | | |
| Reinstatement Proposal for Temporary Steel Cofferdam & Double Water Gate System | | | | | | | | | | | | 2018 | | | | | 2018 | |
| S13889-06 | Resubmit to Reinstatement Proposal for Temporary Steel Cofferdam & Water Gate System (CE057) | P2-Cal.A | 18 | 3 | 21-Sep-17 A | 22-Oct-17 | -284 | 83.33% | 15 | | | | | | | | | |
| S13889-07 | Accept of Reinstatement Proposal for Temporary Steel Cofferdam & Water Gate System (CE057) | P2-Cal.A | 9 | 9 | 23-Oct-17 | 31-Oct-17 | -284 | 0% | 0 | | | | | | | | | |
| Installation of Pre-Bored Socketed H-Pile (Reclaimed Section) | | | | | | | | | | | | 2018 | | | | | 2018 | |
| S13970 | Prepare and Submit Method Statement for Installation of Pre-bored Socket H-Pile (Reclaimed Section) | P2-Cal.A | 7 | 7 | 22-Dec-17 | 28-Dec-17 | -29 | 0% | 0 | | | | | | | | | |
| S13971 | Review and Discuss Method Statement for Installation of Pre-bored Socket H-Pile(Reclaimed Section) | P2-Cal.A | 21 | 21 | 30-Dec-17 | 19-Jan-18 | -29 | 0% | 0 | | | | | | | | | |
| ELS of Underpass (P2 CH105-318) | | | | | | | | | | | | 2018 | | | | | 2018 | |
| S14056 | Prepare and Submit Method Statement for Excavation and ELS of Underpass (P2 CH105-318) | P2-Cal.A | 18 | 18 | 10-Nov-17 | 27-Nov-17 | 91 | 0% | 0 | | | | | | | | | |
| S14057 | 1st Review and Discuss Method Statement for Excavation and ELS of Underpass (P2 CH105-318) | P2-Cal.A | 21 | 21 | 28-Nov-17 | 18-Dec-17 | 91 | 0% | 0 | | | | | | | | | |
| S14058 | Resubmit Method Statement for Excavation and ELS of Underpass (P2 CH105-318) | P2-Cal.A | 7 | 7 | 19-Dec-17 | 25-Dec-17 | 91 | 0% | 0 | | | | | | | | | |
| S14059 | Accept Method Statement for Excavation and ELS of Underpass (P2 CH105-318) | P2-Cal.A | 21 | 21 | 26-Dec-17 | 15-Jan-18 | 91 | 0% | 0 | | | | | | | | | |
| ELS of U-Troughs (P2 CH318-363) | | | | | | | | | | | | 2018 | | | | | 2018 | |
| S14060 | Prepare and Submit Method Statement for Excavation and ELS of U-Troughs (P2 CH318-363) | P2-Cal.A | 18 | 18 | 08-Dec-17 | 25-Dec-17 | -21 | 0% | 0 | | | | | | | | | |
| S14080 | 1st Review and Discuss Method Statement for Excavation and ELS of U-Troughs (P2 CH318-363) | P2-Cal.A | 21 | 21 | 26-Dec-17 | 15-Jan-18 | -21 | 0% | 0 | | | | | | | | | |
| S14100 | Resubmit Method Statement for Excavation and ELS of U-Troughs (P2 CH318-363) | P2-Cal.A | 7 | 7 | 16-Jan-18 | 22-Jan-18 | -21 | 0% | 0 | | | | | | | | | |
| Construction of U-Troughs structure (P2 CH411-500) | | | | | | | | | | | | 2018 | | | | | 2018 | |
| S14200 | Accept Method Statement for Construction of U-Troughs Structure (P2 CH411-500) | P2-Cal.A | 21 | 10 | 20-Oct-17 A | 29-Oct-17 | 247 | 52.38% | 25 | | | | | | | | | |

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Oct-17)

3 Months Rolling Programme
 (20 October 2017)
 Page: 4 of 11

| Date | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 20-Oct-17 | | | |

| Activity ID | Activity Name | Calendar | Original Duration | Remaining Duration | Start | Finish | Total Float | Activity % Complete | Variance - BL1 Finish Date | TRA | 2017 | | | | | 2018 | | |
|---|--|----------|-------------------|--------------------|-------------|-----------|-------------|---------------------|----------------------------|-----|------|--|-----|-----|-----|------|-----|--|
| | | | | | | | | | | | Oct | Nov | Dec | Jan | Feb | Jan | Feb | |
| Treatment of Dredged Marine Sediment of Type 1 | | | | | | | | | | | | Treatment of Dredged Marine Sediment of Type 1 | | | | | | |
| S14373-1 | Submit Method Statement for Treatment of Dredging Marine Sediment of Type 1 | P2-Cal.A | 21 | 4 | 15-Sep-17 A | 23-Oct-17 | -282 | 80.95% | 17 | | | | | | | | | |
| S14374 | Review and Accept Method Statement for Treatment of Dredging Marine Sediment of Type 1 | P2-Cal.A | 10 | 10 | 24-Oct-17 | 02-Nov-17 | -282 | 0% | 0 | | | | | | | | | |
| Construction of Vertical Seawall | | | | | | | | | | | | Construction of Vertical Seawall | | | | | | |
| S14931 | Prepare and Submit Method Statement for Construction of Vertical Seawall | P2-Cal.A | 18 | 18 | 11-Dec-17 | 28-Dec-17 | -249 | 0% | 0 | | | | | | | | | |
| S14933 | Review and Discuss Method Statement for Construction of Vertical Seawall | P2-Cal.A | 21 | 21 | 29-Dec-17 | 18-Jan-18 | -249 | 0% | 0 | | | | | | | | | |
| S14935 | Resubmit Method Statement for Construction of Vertical Seawall | P2-Cal.A | 14 | 14 | 19-Jan-18 | 01-Feb-18 | -249 | 0% | 0 | | | | | | | | | |
| Construction of Vertical Band Drain | | | | | | | | | | | | Construction of Vertical Band Drain | | | | | | |
| S14939 | Prepare and Submit Method Statement for Construction of Vertical Band Drain | P2-Cal.A | 5 | 5 | 11-Nov-17 | 15-Nov-17 | -229 | 0% | 0 | | | | | | | | | |
| S14941 | Review and Discuss Method Statement for Construction of Vertical Band Drain | P2-Cal.A | 21 | 21 | 16-Nov-17 | 06-Dec-17 | -229 | 0% | 0 | | | | | | | | | |
| S14945 | Resubmit Method Statement for Construction of Vertical Band Drain | P2-Cal.A | 3 | 3 | 07-Dec-17 | 09-Dec-17 | -229 | 0% | 0 | | | | | | | | | |
| S14947 | Accept Method Statement for Construction of Vertical Band Drain | P2-Cal.A | 14 | 14 | 10-Dec-17 | 23-Dec-17 | -229 | 0% | 0 | | | | | | | | | |
| Construction of DN2100 | | | | | | | | | | | | Construction of DN2100 | | | | | | |
| S14961 | Resubmit Method Statement for Construction of DN2100 | P2-Cal.A | 14 | 0 | 24-May-17 A | 20-Oct-17 | -21 | 100% | -135 | | | | | | | | | |
| S14962 | Accept Method Statement for Construction of DN2100 | P2-Cal.A | 21 | 21 | 20-Oct-17 | 09-Nov-17 | -21 | 0% | 0 | | | | | | | | | |
| Procurement of Major Material | | | | | | | | | | | | Procurement of Major Material | | | | | | |
| Civil/Structural | | | | | | | | | | | | Civil/Structural | | | | | | |
| S14981 | Procurement and Delivery of Steel H-Pile | P2-Cal.A | 800 | 570 | 31-Jan-17 A | 12-May-19 | -280 | 28.75% | -32 | | | | | | | | | |
| S14983 | Procurement and Delivery of ELS Waling & Struts Members | P2-Cal.A | 1015 | 804 | 20-Jan-17 A | 01-Jan-20 | -280 | 20.79% | -62 | | | | | | | | | |
| S14985 | Offsite Fabrication of Pre-cast Seawall blocks | P2-Cal.A | 40 | 40 | 27-Dec-17 | 04-Feb-18 | -229 | 0% | 0 | | | | | | | | | |
| S14995 | Offsite Fabrication of Marine Survey Tower | P2-Cal.A | 120 | 120 | 02-Jan-18 | 01-May-18 | -270 | 0% | 0 | | | | | | | | | |
| S15001 | Procurement and Delivery of 1500DN materials | P2-Cal.A | 90 | 90 | 02-Jan-18 | 01-Apr-18 | -111 | 0% | 0 | | | | | | | | | |
| Architectural | | | | | | | | | | | | Architectural | | | | | | |
| S15142 | Procurement and Delivery of V-Panel / Precast Concrete Panel | P2-Cal.A | 450 | 450 | 05-Jan-18 | 30-Mar-19 | 232 | 0% | 0 | | | | | | | | | |
| S15143 | Precast Concrete Road Profile Barrier | P2-Cal.A | 180 | 180 | 11-Nov-17 | 09-May-18 | 335 | 0% | 0 | | | | | | | | | |
| Subletting Package | | | | | | | | | | | | Subletting Package | | | | | | |
| V Panel and Precast Concrete Panel | | | | | | | | | | | | V Panel and Precast Concrete Panel | | | | | | |
| S15156 | Tender Interview and Recommendation to PM for V Panel and Precast Concrete Panel (Re-tender due to revise dwg) | P2-Cal.A | 21 | 21 | 15-Dec-17 | 04-Jan-18 | 232 | 0% | 0 | | | | | | | | | |
| S15160 | V Panel and Precast Concrete Panel Award | P2-Cal.A | 0 | 0 | | 04-Jan-18 | 232 | 0% | 0 | | | | | | | | | |
| Structural Works for U-Trough, Underpass and Abutment | | | | | | | | | | | | Structural Works for U-Trough, Underpass and Abutment | | | | | | |
| S16400 | Prepare Structural Works for U-Trough, Underpass and Abutment Tender Document for PM Acceptance | P2-Cal.A | 60 | 40 | 01-Sep-17 A | 28-Nov-17 | 315 | 33.33% | -8 | | | | | | | | | |
| S16420 | Invitation, Submission and Opening of Tender for Structural Works for U-Trough, Underpass and Abutment | P2-Cal.A | 60 | 60 | 29-Nov-17 | 27-Jan-18 | 315 | 0% | 0 | | | | | | | | | |
| Drainage and Sewerage Works (Existing Land) (Inside U trough) | | | | | | | | | | | | Drainage and Sewerage Works (Existing Land) (Inside U trough) | | | | | | |
| S17080 | Tender Interview and Recommendation to PM for Drainage and Sewerage Works | P2-Cal.A | 21 | 4 | 03-Sep-17 A | 23-Oct-17 | 253 | 80.95% | 1 | | | | | | | | | |
| S17100 | Drainage and Sewerage Works Award | P2-Cal.A | 0 | 0 | | 23-Oct-17 | 253 | 0% | 0 | | | | | | | | | |
| Drainage and Sewerage Works (Existing Land) (At Grade Section) | | | | | | | | | | | | Drainage and Sewerage Works (Existing Land) (At Grade Section) | | | | | | |
| S17104 | Submission and Opening of Tender for Drainage and Sewerage Works | P2-Cal.A | 42 | 42 | 27-Apr-17 A | 30-Nov-17 | 399 | 0% | -176 | | | | | | | | | |
| S17106 | Tender Interview and Recommendation to PM for Drainage and Sewerage Works | P2-Cal.A | 21 | 21 | 01-Dec-17 | 21-Dec-17 | 399 | 0% | 0 | | | | | | | | | |
| S17108 | Drainage and Sewerage Works Award | P2-Cal.A | 0 | 0 | | 21-Dec-17 | 399 | 0% | 0 | | | | | | | | | |
| Drainage and Sewerage Works (Reclaimed Section) | | | | | | | | | | | | Drainage and Sewerage Works (Reclaimed Section) | | | | | | |
| S17110 | Prepare Drainage and Sewerage Works Tender Document for PM Acceptance | P2-Cal.A | 30 | 3 | 19-Aug-17 A | 22-Oct-17 | 806 | 90% | -156 | | | | | | | | | |
| S17112 | Submission and Opening of Tender for Drainage and Sewerage Works | P2-Cal.A | 14 | 14 | 23-Oct-17 | 05-Nov-17 | 806 | 0% | 0 | | | | | | | | | |
| S17114 | Tender Interview and Recommendation to PM for Drainage and Sewerage Works | P2-Cal.A | 21 | 21 | 06-Nov-17 | 26-Nov-17 | 806 | 0% | 0 | | | | | | | | | |
| S17116 | Drainage and Sewerage Works Award | P2-Cal.A | 0 | 0 | | 26-Nov-17 | 806 | 0% | 0 | | | | | | | | | |
| Water Works (To be Incorporated in Irrigation Package) | | | | | | | | | | | | Water Works (To be Incorporated in Irrigation Package) | | | | | | |
| S17120 | Prepare Water Works Tender Document for PM Acceptance | P2-Cal.A | 30 | 24 | 07-Aug-17 A | 12-Nov-17 | 426 | 20% | -55 | | | | | | | | | |
| S17140 | Submission and Opening of Tender for Water Works | P2-Cal.A | 30 | 30 | 13-Nov-17 | 12-Dec-17 | 426 | 0% | 0 | | | | | | | | | |

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Oct-17)

3 Months Rolling Programme
 (20 October 2017)
 Page: 5 of 11

| Date | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 20-Oct-17 | | | |

| Activity ID | Activity Name | Calendar | Original Duration | Remaining Duration | Start | Finish | Total Float | Activity % Complete | Variance - BL1 Finish Date | TRA | 2017 | | | | | 2018 | |
|--|---|----------|-------------------|--------------------|-------------|------------|-------------|---------------------|----------------------------|-----|------|-----|-----|-----|-----|------|---|
| | | | | | | | | | | | Oct | Nov | Dec | Jan | Feb | | |
| S17160 | Tender Interview and Recommendation to PM for Water Works | P2-Cal.A | 21 | 21 | 13-Dec-17 | 02-Jan-18 | 426 | 0% | 0 | | | | | | | | Tender Interview and Recommendation |
| S17180 | Water Works Award | P2-Cal.A | 0 | 0 | | 02-Jan-18 | 426 | 0% | 0 | | | | | | | | ◆ Water Works Award |
| Irrigation Works | | P2-Cal.A | 103 | 73 | 07-Aug-17 A | 31-Dec-17 | 609 | | 0 | | | | | | | | Irrigation Works |
| S17280 | Prepare Irrigation Works Tender Document for PM Acceptance | P2-Cal.A | 30 | 24 | 07-Aug-17 A | 12-Nov-17 | 609 | 20% | -24 | | | | | | | | Prepare Irrigation Works Tender Document for PM Acceptance |
| S17300 | Submission and Opening of Tender for Irrigation Works | P2-Cal.A | 28 | 28 | 13-Nov-17 | 10-Dec-17 | 609 | 0% | 0 | | | | | | | | Submission and Opening of Tender for Irrigation Works |
| S17320 | Tender Interview and Recommendation to PM for Irrigation Works | P2-Cal.A | 21 | 21 | 11-Dec-17 | 31-Dec-17 | 609 | 0% | 0 | | | | | | | | Tender Interview and Recommendation |
| S17340 | Irrigation Works Award | P2-Cal.A | 0 | 0 | | 31-Dec-17 | 609 | 0% | 0 | | | | | | | | ◆ Irrigation Works Award |
| E & M Work (Electrical) | | P2-Cal.A | 21 | 21 | 06-Jan-18 | 26-Jan-18 | 22 | | 0 | | | | | | | | E & M Work (Elec |
| S17400 | Tender Interview and Recommendation to PM for E & M Works (Electrical) | P2-Cal.A | 21 | 21 | 06-Jan-18 | 26-Jan-18 | 22 | 0% | 0 | | | | | | | | Tender Interview a |
| E & M Works (MVAC) | | P2-Cal.A | 160 | 48 | 30-Jun-17 A | 06-Dec-17 | 33 | | 0 | | | | | | | | E & M Works (MVAC) |
| S17422 | Prepare E & M Works (MVAC) Tender Document for PM Acceptance | P2-Cal.A | 57 | 6 | 30-Jun-17 A | 25-Oct-17 | 33 | 89.47% | -61 | | | | | | | | Prepare E & M Works (MVAC) Tender Document for PM Acceptance |
| S17423 | Submission and Opening of Tender for E & M Works (MVAC) | P2-Cal.A | 21 | 21 | 26-Oct-17 | 15-Nov-17 | 33 | 0% | 0 | | | | | | | | Submission and Opening of Tender for E & M Works (MVAC) |
| S17424 | Tender Interview and Recommendation to PM for E & M Works (MVAC) | P2-Cal.A | 21 | 21 | 16-Nov-17 | 06-Dec-17 | 33 | 0% | 0 | | | | | | | | Tender Interview and Recommendation to PM for E & M W |
| S17425 | E & M Works Award (MVAC) | P2-Cal.A | 0 | 0 | | 06-Dec-17 | 33 | 0% | 0 | | | | | | | | ◆ E & M Works Award (MVAC) |
| E & M Works (FS) | | P2-Cal.A | 160 | 33 | 15-Aug-17 A | 13-Dec-17 | 66 | | 0 | | | | | | | | E & M Works (FS) |
| S17427 | Submission and Opening of Tender for E & M Works (FS) | P2-Cal.A | 14 | 12 | 15-Aug-17 A | 22-Nov-17 | 66 | 14.29% | -125 | | | | | | | | Submission and Opening of Tender for E & M Works (FS) |
| S17428 | Tender Interview and Recommendation to PM for E & M Works (FS) | P2-Cal.A | 21 | 21 | 23-Nov-17 | 13-Dec-17 | 66 | 0% | 0 | | | | | | | | Tender Interview and Recommendation to PM for E & |
| S17429 | E & M Works (FS) Award | P2-Cal.A | 0 | 0 | | 13-Dec-17 | 66 | 0% | 0 | | | | | | | | ◆ E & M Works (FS) Award |
| E & M Works (Plumbing & Drainage) | | P2-Cal.A | 109 | 48 | 20-Aug-17 A | 06-Dec-17 | 33 | | 0 | | | | | | | | E & M Works (Plumbing & Drainage) |
| S17430 | Prepare E & M Works (Plumbing & Drainage) Tender Document for PM Acceptance | P2-Cal.A | 40 | 13 | 20-Aug-17 A | 01-Nov-17 | 33 | 67.5% | -34 | | | | | | | | Prepare E & M Works (Plumbing & Drainage) Tender Document for PM Acceptance |
| S17431 | Submission and Opening of Tender for E & M Works (Plumbing & Drainage) | P2-Cal.A | 14 | 14 | 02-Nov-17 | 15-Nov-17 | 33 | 0% | 0 | | | | | | | | Submission and Opening of Tender for E & M Works (Plumbing & Drainage) |
| S17432 | Tender Interview and Recommendation to PM for E & M Works (Plumbing & Drainage) | P2-Cal.A | 21 | 21 | 16-Nov-17 | 06-Dec-17 | 33 | 0% | 0 | | | | | | | | Tender Interview and Recommendation to PM for E & M W |
| S17433 | E & M Works (Plumbing & Drainage) Award | P2-Cal.A | 0 | 0 | | 06-Dec-17 | 33 | 0% | 0 | | | | | | | | ◆ E & M Works (Plumbing & Drainage) Award |
| Section 1 of the Works | | | 274 | 72 | 01-Apr-17 A | 30-Dec-17 | 0 | | 0 | | | | | | | | Section 1 of the Works |
| Reprovisioning of DSD Transformer Room | | | 274 | 72 | 01-Apr-17 A | 30-Dec-17 | 0 | | 0 | | | | | | | | Reprovisioning of DSD Transformer Roc |
| Foundation Works | | P2-Cal.A | 0 | 0 | 30-Dec-17 | 30-Dec-17 | 0 | | 0 | | | | | | | | ▼ Foundation Works |
| LC10470 | CE no.026: Upkeeping of Portion III of the Site | P2-Cal.A | 0 | 0 | | 30-Dec-17* | 0 | 0% | 0 | | | | | | | | ◆ CE no.026: Upkeeping of Portion III of if |
| Draw Pit Construction | | P2-Cal.C | 181 | 18 | 01-Apr-17 A | 10-Nov-17 | 22 | | 0 | | | | | | | | Draw Pit Construction |
| LC10919 | Construction of 3 nos. ATC Drawpits (PMI No.4 and 11) | P2-Cal.C | 5 | 3 | 13-Sep-17 A | 23-Oct-17 | 32 | 40% | -16 | | | | | | | | Construction of 3 nos. ATC Drawpits (PMI No.4 and 11) |
| LC10921 | Construction of 3 nos. Earthing Pits (PMI No.4 and 11) | P2-Cal.C | 5 | 5 | 20-Sep-17 A | 30-Oct-17 | 32 | 0% | -22 | | | | | | | | Construction of 3 nos. Earthing Pits (PMI No.4 and 11) |
| LC10923 | Backfilling of cable duct after installation | P2-Cal.C | 21 | 8 | 01-Apr-17 A | 30-Oct-17 | 19 | 61.9% | -150 | | | | | | | | Backfilling of cable duct after installation |
| LC10927 | Road Pavement Works (RFI 017--- PMI 030) (Incl. reinstatement, road formation, Kerb Installation) | P2-Cal.C | 10 | 10 | 31-Oct-17 | 10-Nov-17 | 19 | 0% | 0 | | | | | | | | Road Pavement Works (RFI 017--- PMI 030) (Incl. reinstatement, road formation |
| Drainage Construction (CE-032) | | P2-Cal.C | 25 | 17 | 20-Sep-17 A | 09-Nov-17 | 23 | | 0 | | | | | | | | Drainage Construction (CE-032) |
| LC10957 | Formwork Haunching | P2-Cal.C | 3 | 2 | 19-Oct-17 A | 21-Oct-17 | 23 | 33.33% | 11 | | | | | | | | Formwork Haunching |
| LC10958 | Concreting | P2-Cal.C | 1 | 1 | 23-Oct-17 | 23-Oct-17 | 23 | 0% | 0 | | | | | | | | Concreting |
| LC10959 | Top Slab Formwork (STMH-B5-01) | P2-Cal.C | 2 | 2 | 24-Oct-17 | 25-Oct-17 | 23 | 0% | 0 | | | | | | | | Top Slab Formwork (STMH-B5-01) |
| LC10960 | Concreting | P2-Cal.C | 1 | 1 | 26-Oct-17 | 26-Oct-17 | 23 | 0% | 0 | | | | | | | | Concreting |
| LC10961 | Laying 375 Drain | P2-Cal.C | 4 | 4 | 27-Oct-17 | 01-Nov-17 | 23 | 0% | 0 | | | | | | | | Laying 375 Drain |
| LC10962 | Backfilling / Reinstatement | P2-Cal.C | 7 | 7 | 02-Nov-17 | 09-Nov-17 | 23 | 0% | 0 | | | | | | | | Backfilling / Reinstatement |
| LC10964 | Excavation | P2-Cal.C | 2 | 2 | 20-Sep-17 A | 21-Oct-17 | 22 | 0% | -8 | | | | | | | | Excavation |
| LC10965 | Blinding Layer | P2-Cal.C | 1 | 1 | 12-Oct-17 A | 23-Oct-17 | 22 | 0% | 0 | | | | | | | | Blinding Layer |
| LC10966 | Formwork Haunching | P2-Cal.C | 2 | 2 | 13-Oct-17 A | 25-Oct-17 | 22 | 0% | 0 | | | | | | | | Formwork Haunching |
| LC10967 | Concreting (SMH-B5-01 to CP-03 & SMH-B5-02) | P2-Cal.C | 1 | 1 | 16-Oct-17 A | 26-Oct-17 | 27 | 0% | 0 | | | | | | | | Concreting (SMH-B5-01 to CP-03 & SMH-B5-02) |
| LC10968 | Top Slab Formwork (SMH-B5-01 to CP-03) | P2-Cal.C | 2 | 2 | 27-Oct-17 | 30-Oct-17 | 27 | 0% | 0 | | | | | | | | Top Slab Formwork (SMH-B5-01 to CP-03) |
| LC10969 | Concreting (SMH-B5-01/SMH-B5-02) | P2-Cal.C | 1 | 1 | 31-Oct-17 | 31-Oct-17 | 27 | 0% | 0 | | | | | | | | Concreting (SMH-B5-01/SMH-B5-02) |
| LC10971 | Backfill and Reinstatement | P2-Cal.C | 4 | 4 | 01-Nov-17 | 04-Nov-17 | 27 | 0% | 0 | | | | | | | | Backfill and Reinstatement |
| BS Installation | | P2-Cal.C | 24 | 24 | 25-Oct-17 | 22-Nov-17 | 19 | | 0 | | | | | | | | BS Installation |

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Oct-17)

3 Months Rolling Programme
 (20 October 2017)
 Page: 6 of 11

| Date | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 20-Oct-17 | | | |

| Activity ID | Activity Name | Calendar | Original Duration | Remaining Duration | Start | Finish | Total Float | Activity % Complete | Variance - BL1 Finish Date | TRA | 2017 | | | | | 2018 | |
|---|--|----------|-------------------|--------------------|-------------|------------|-------------|---------------------|----------------------------|-----|------|-----|-----|-----|-----|------|-----|
| | | | | | | | | | | | Oct | Nov | Dec | Jan | Feb | Jan | Feb |
| FS | | P2-Cal.C | 24 | 24 | 25-Oct-17 | 22-Nov-17 | 19 | | | | | | | | | | |
| LC11084 | 2nd Submit Form 314/501 | P2-Cal.C | 0 | 0 | | 25-Oct-17 | 19 | 0% | 0 | | | | | | | | |
| LC11085 | FSD Inspection | P2-Cal.C | 0 | 0 | 15-Nov-17 | | 19 | 0% | 0 | | | | | | | | |
| LC11087 | Issue Fire Certificate | P2-Cal.C | 0 | 0 | | 22-Nov-17 | 19 | 0% | 0 | | | | | | | | |
| Road Works | | P2-Cal.C | 10 | 10 | 31-Oct-17 | 10-Nov-17 | 41 | | | | | | | | | | |
| LC11091 | PMI 030 Road Furniture Works (Incl. signages) | P2-Cal.C | 10 | 10 | 31-Oct-17 | 10-Nov-17 | 41 | 0% | 0 | | | | | | | | |
| LC11093 | Installation of Chain Link Fence, Vehicle Gate - 2 gates | P2-Cal.C | 3 | 3 | 08-Nov-17 | 10-Nov-17 | 41 | 0% | 0 | | | | | | | | |
| Demolition of Existing DSD Transformer Room | | | 43 | 53 | 16-Oct-17 A | 11-Dec-17 | 19 | | | | | | | | | | |
| LC11095 | Handover to DSD | P2-Cal.C | 0 | 0 | 23-Nov-17 | | 31 | 0% | 0 | | | | | | | | |
| LC11097 | Decommission existing DSD Tx Room by CLP | P2-Cal.A | 10 | 10 | 16-Oct-17 A | 29-Oct-17 | 17 | 0% | 35 | | | | | | | | |
| LC11099 | Demolish existing DSD Tx Room | P2-Cal.C | 25 | 25 | 30-Oct-17 | 27-Nov-17 | 15 | 0% | 0 | | | | | | | | |
| LC11101 | Reinstatement of demolished DSD Tx Room | P2-Cal.C | 12 | 12 | 28-Nov-17 | 11-Dec-17 | 15 | 0% | 0 | | | | | | | | |
| Section 3 of the Works All Works within Portion IV, V, VI, VII, VIII, and IX | | | 550 | 382 | 05-May-17 A | 05-Nov-18 | 232 | | | | | | | | | | |
| Existing Land Section | | | 533 | 365 | 05-May-17 A | 19-Oct-18 | 249 | | | | | | | | | | |
| Retaining Wall P2-A CH 500- 650 | | | 518 | 365 | 20-May-17 A | 19-Oct-18 | 249 | | | | | | | | | | |
| LC11925 | Submission and Approval from LCSD for removal of existing planter (NCE-019 & EW-014) by PM | P2-Cal.A | 200 | 47 | 20-May-17 A | 05-Dec-17 | -102 | 76.5% | 0 | | | | | | | | |
| LC11926 | Trial Pit of underground utilities | P2-Cal.C | 6 | 6 | 06-Dec-17 | 12-Dec-17 | 258 | 0% | 0 | | | | | | | | |
| LC11928 | Confirmation CLP cable Diversion and relocation of WSD flowmeter chamber (by others) (NCE-029) (NCE-030) (PMI-027) | P2-Cal.A | 0 | 0 | | 20-Oct-17* | -111 | 0% | 0 | | | | | | | | |
| LC11929 | CLP cable Diversion and relocation of WSD flowmeter chamber (by others) (NCE-029) (NCE-030) (PMI-027) | P2-Cal.A | 365 | 365 | 20-Oct-17 | 19-Oct-18 | -102 | 0% | 0 | | | | | | | | |
| Bay 3-4 | | P2-Cal.C | 23 | 23 | 09-Oct-17 A | 16-Nov-17 | 472 | | | | | | | | | | |
| LC11955 | Construction of RW P2-A Wall Stem - Bay 3 (Team B) | P2-Cal.C | 10 | 7 | 09-Oct-17 A | 27-Oct-17 | 472 | 30% | 3 | | | | | | | | |
| LC11957 | Waterproofing coating Works RW P2-A (Bay 3 - 4) | P2-Cal.C | 6 | 6 | 30-Oct-17 | 04-Nov-17 | 472 | 0% | 0 | | | | | | | | |
| LC11958 | Backfilling Works RW P2-A Back Side (Bay 3 - 4) (Incl. soil test) | P2-Cal.C | 10 | 10 | 06-Nov-17 | 16-Nov-17 | 472 | 0% | 0 | | | | | | | | |
| P2 Road | | P2-Cal.C | 244 | 104 | 05-May-17 A | 26-Feb-18 | 243 | | | | | | | | | | |
| P2 CH 318 - 363 | | P2-Cal.C | 244 | 104 | 05-May-17 A | 26-Feb-18 | -115 | | | | | | | | | | |
| TTA Stage 1 - TTA for Temp Road Construction for P2 CH318-399 | | P2-Cal.C | 5 | 5 | 05-May-17 A | 25-Oct-17 | -76 | | -140 | | | | | | | | |
| LC12760 | Remove road lighting and street furnitures (Road lighting pending HyD) | P2-Cal.C | 5 | 5 | 05-May-17 A | 25-Oct-17 | -76 | 0% | -140 | | | | | | | | |
| Foundation P2 CH318-363 | | P2-Cal.C | 58 | 58 | 20-Sep-17 A | 29-Dec-17 | -69 | | 0 | | | | | | | | |
| LC12887 | Trial Pit Excavation for Pre-bored socket H-Pile (A11-A18) (8nos) | P2-Cal.C | 15 | 9 | 25-Sep-17 A | 31-Oct-17 | -115 | 40% | 10 | | | | | | | | |
| LC12888 | Construction of Stage 2 Temp. Road for Portion VI | P2-Cal.C | 13 | 7 | 20-Sep-17 A | 27-Oct-17 | -113 | 46.15% | 6 | | | | | | | | |
| LC12895 | Installation of Pre-bored socket H-Pile (A19) (Rig A) | P2-Cal.C | 5 | 5 | 01-Nov-17 | 06-Nov-17 | -64 | 0% | 0 | | | | | | | | |
| LC12896 | Installation of Pre-bored socket H-Pile (A7) (Rig A) | P2-Cal.C | 5 | 5 | 07-Nov-17 | 11-Nov-17 | -64 | 0% | 0 | | | | | | | | |
| LC12897 | Installation of Pre-bored socket H-Pile (A16) (Rig A) | P2-Cal.C | 5 | 5 | 13-Nov-17 | 17-Nov-17 | -64 | 0% | 0 | | | | | | | | |
| LC12898 | Installation of Pre-bored socket H-Pile (A12) (Rig A) | P2-Cal.C | 5 | 5 | 18-Nov-17 | 23-Nov-17 | -64 | 0% | 0 | | | | | | | | |
| LC12899 | Installation of Pre-bored socket H-Pile (A17) (Rig A) | P2-Cal.C | 5 | 5 | 24-Nov-17 | 29-Nov-17 | -64 | 0% | 0 | | | | | | | | |
| LC12900 | Installation of Pre-bored socket H-Pile (A13) (Rig A) | P2-Cal.C | 5 | 5 | 30-Nov-17 | 05-Dec-17 | -64 | 0% | 0 | | | | | | | | |
| LC12902 | Installation of Pre-bored socket H-Pile (A18) (Rig B) | P2-Cal.C | 5 | 5 | 01-Nov-17 | 06-Nov-17 | -115 | 0% | 0 | | | | | | | | |
| LC12903 | Installation of Pre-bored socket H-Pile (A9) (Rig B) | P2-Cal.C | 5 | 5 | 07-Nov-17 | 11-Nov-17 | -115 | 0% | 0 | | | | | | | | |
| LC12904 | Installation of Pre-bored socket H-Pile (A14) (Rig B) | P2-Cal.C | 5 | 5 | 13-Nov-17 | 17-Nov-17 | -115 | 0% | 0 | | | | | | | | |
| LC12905 | Installation of Pre-bored socket H-Pile (A10) (Rig B) | P2-Cal.C | 5 | 5 | 18-Nov-17 | 23-Nov-17 | -115 | 0% | 0 | | | | | | | | |
| LC12906 | Installation of Pre-bored socket H-Pile (A15) (Rig B) | P2-Cal.C | 5 | 5 | 24-Nov-17 | 29-Nov-17 | -115 | 0% | 0 | | | | | | | | |
| LC12907 | Installation of Pre-bored socket H-Pile (A11) (Rig B) | P2-Cal.C | 5 | 5 | 30-Nov-17 | 05-Dec-17 | -115 | 0% | 0 | | | | | | | | |
| LC12908 | Installation of Pre-bored socket H-Pile (A6) (Rig B) | P2-Cal.C | 5 | 5 | 06-Dec-17 | 11-Dec-17 | -115 | 0% | 0 | | | | | | | | |
| LC12928 | Construction of temporary lighting ducting and removal of existing street light | P2-Cal.C | 30 | 30 | 30-Oct-17 | 02-Dec-17 | -113 | 0% | 0 | | | | | | | | |
| LC12948 | Construction of temporary road for stage 2B TTA | P2-Cal.C | 14 | 14 | 12-Dec-17 | 29-Dec-17 | -69 | 0% | 0 | | | | | | | | |
| ELS P2 CH318-363 & SR2 CH100-110 | | P2-Cal.C | 67 | 67 | 04-Dec-17 | 26-Feb-18 | -115 | | 0 | | | | | | | | |
| LC12950 | Plant Mobilization | P2-Cal.C | 5 | 5 | 04-Dec-17 | 08-Dec-17 | -113 | 0% | 0 | | | | | | | | |

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Oct-17)

3 Months Rolling Programme
 (20 October 2017)
 Page: 7 of 11

| Date | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 20-Oct-17 | | | |

| Activity ID | Activity Name | Calendar | Original Duration | Remaining Duration | Start | Finish | Total Float | Activity % Complete | Variance - BL1 Finish Date | TRA | 2017 | | | | | 2018 | |
|--|---|----------|-------------------|--------------------|-------------|-----------|-------------|---------------------|----------------------------|-----|------|-----|-----|-----|-----|------|-----|
| | | | | | | | | | | | Oct | Nov | Dec | Jan | Feb | Jan | Feb |
| LC12951 | Overcome obstruction by Pre-bore method at CH318-363 (176m)(EW-019)(CE-020) | P2-Cal.C | 60 | 60 | 12-Dec-17 | 26-Feb-18 | -115 | 0% | | | | | | | | | |
| P2 CH 411 - 500 | | P2-Cal.C | 79 | 79 | 14-Oct-17 A | 24-Jan-18 | 268 | | | | | | | | | | |
| ELS P2 CH 411 - 500 | | P2-Cal.C | 10 | 10 | 20-Oct-17 | 01-Nov-17 | 329 | | | | | | | | | | |
| Construction of ELS works, P2 CH411 to CH500 | | P2-Cal.C | 10 | 10 | 20-Oct-17 | 01-Nov-17 | 329 | | | | | | | | | | |
| 3rd Stage ELS Construction (-0.5.mPD) | | P2-Cal.C | 10 | 10 | 20-Oct-17 | 01-Nov-17 | 329 | | | | | | | | | | |
| LC14649 | Pile head installation between P2 CH411 and CH423 (9nos) | P2-Cal.C | 10 | 10 | 20-Oct-17 | 01-Nov-17 | 329 | 0% | | | | | | | | | |
| Structure P2 CH 411 - 500 (U Trough A) | | P2-Cal.C | 79 | 79 | 14-Oct-17 A | 24-Jan-18 | 268 | | | | | | | | | | |
| LC14705 | Laying Blinding at Bay 2 to Bay 4 | P2-Cal.C | 7 | 7 | 14-Oct-17 A | 27-Oct-17 | 232 | 0% | 7 | | | | | | | | |
| LC14710 | Laying Blinding at Bay 1 | P2-Cal.C | 3 | 3 | 08-Nov-17 | 10-Nov-17 | 329 | 0% | | | | | | | | | |
| LC14720 | Waterproofing Works at Bay 6 | P2-Cal.C | 2 | 2 | 20-Oct-17 | 21-Oct-17 | 203 | 0% | | | | | | | | | |
| LC14740 | Construction of Base Slab & drainage at Bay 6 (CH475 - 488) | P2-Cal.C | 16 | 16 | 30-Oct-17 | 16-Nov-17 | 198 | 0% | | | | | | | | | |
| LC14760 | Construction of Wall Stem at Bay 6 (CH475 - 488) | P2-Cal.C | 18 | 18 | 17-Nov-17 | 07-Dec-17 | 198 | 0% | | | | | | | | | |
| LC14770 | Waterproofing Works at Bay 4 | P2-Cal.C | 2 | 2 | 30-Oct-17 | 31-Oct-17 | 232 | 0% | | | | | | | | | |
| LC14780 | Construction of Base Slab & drainage at Bay 4 (CH449 - 462) | P2-Cal.C | 16 | 16 | 01-Nov-17 | 18-Nov-17 | 232 | 0% | | | | | | | | | |
| LC14800 | Construction of Wall Stem at Bay 4 (CH449 - 462) | P2-Cal.C | 18 | 18 | 20-Nov-17 | 09-Dec-17 | 232 | 0% | | | | | | | | | |
| LC14810 | Waterproofing Works at Bay 7 | P2-Cal.C | 2 | 2 | 08-Dec-17 | 09-Dec-17 | 198 | 0% | | | | | | | | | |
| LC14820 | Construction of Base Slab & drainage at Bay 7 (CH488 - 500) | P2-Cal.C | 16 | 16 | 11-Dec-17 | 30-Dec-17 | 198 | 0% | | | | | | | | | |
| LC14840 | Construction of Wall Stem at Bay 7 (CH488 - 500) | P2-Cal.C | 18 | 18 | 02-Jan-18 | 22-Jan-18 | 198 | 0% | | | | | | | | | |
| LC14850 | Waterproofing Works at Bay 5 | P2-Cal.C | 2 | 2 | 11-Dec-17 | 12-Dec-17 | 232 | 0% | | | | | | | | | |
| LC14860 | Construction of Base Slab & drainage at Bay 5 (CH462 - 475) | P2-Cal.C | 16 | 16 | 13-Dec-17 | 03-Jan-18 | 232 | 0% | | | | | | | | | |
| LC14880 | Construction of Wall Stem at Bay 5 (CH462 - 475) | P2-Cal.C | 18 | 18 | 04-Jan-18 | 24-Jan-18 | 232 | 0% | | | | | | | | | |
| LC14965 | Mass Concrete at Bay 1 (CH423) | P2-Cal.C | 5 | 5 | 02-Nov-17 | 07-Nov-17 | 329 | 0% | | | | | | | | | |
| SR2 | | P2-Cal.C | 130 | 130 | 27-Sep-17 A | 28-Mar-18 | 319 | | | | | | | | | | |
| Retaining Wall SR2-A & B CH250 - 310 | | P2-Cal.C | 13 | 13 | 17-Oct-17 A | 04-Nov-17 | 436 | | | | | | | | | | |
| Retaining Wall SR2-A | | P2-Cal.C | 13 | 13 | 17-Oct-17 A | 04-Nov-17 | 436 | | | | | | | | | | |
| LC16960 | Construction of Base Slab (SR2-A Bay 2) (Team E) | P2-Cal.C | 10 | 3 | 17-Oct-17 A | 23-Oct-17 | 436 | 70% | 7 | | | | | | | | |
| LC16980 | Construction of Wall Stem (SR2-A Bay 2) (Team E) | P2-Cal.C | 10 | 10 | 24-Oct-17 | 04-Nov-17 | 436 | 0% | | | | | | | | | |
| SR2 CH170 - 250 | | P2-Cal.C | 124 | 130 | 27-Sep-17 A | 28-Mar-18 | 319 | | | | | | | | | | |
| ELS | | P2-Cal.C | 20 | 10 | 27-Sep-17 A | 01-Nov-17 | 319 | | 16 | | | | | | | | |
| LC17180 | Excavation and install shoring system (6d) (Total: 4125m3 - 300m3/day) (Bay 4-6) | P2-Cal.C | 20 | 10 | 27-Sep-17 A | 01-Nov-17 | 319 | 50% | 16 | | | | | | | | |
| LC17190 | Open Excavation (Total: 4125m3 - 300m3/day) (Bay 1-3) | P2-Cal.C | 14 | 10 | 27-Sep-17 A | 01-Nov-17 | 319 | 28.57% | 10 | | | | | | | | |
| Structure SR2 CH 170 - 250 (U Trough A) | | P2-Cal.C | 120 | 120 | 02-Nov-17 | 28-Mar-18 | 319 | | | | | | | | | | |
| LC17200 | Construction of Structure SR2 CH170-250 (U trough A) Total 6 bays - 2 teams | P2-Cal.C | 120 | 120 | 02-Nov-17 | 28-Mar-18 | 319 | 0% | | | | | | | | | |
| Portion IV & VII | | P2-Cal.C | 199 | 181 | 17-Aug-17 A | 02-Jun-18 | -163 | | | | | | | | | | |
| Construction of DN2100 stormwater at Portion IV & VII | | P2-Cal.C | 199 | 181 | 17-Aug-17 A | 02-Jun-18 | -163 | | | | | | | | | | |
| Preboring | | P2-Cal.C | 199 | 181 | 18-Sep-17 A | 02-Jun-18 | -183 | | | | | | | | | | |
| Rig 1 | | P2-Cal.C | 199 | 181 | 18-Sep-17 A | 02-Jun-18 | -183 | | | | | | | | | | |
| LC17663 | Stage 4 -- Preboring along Existing EVA to BMPC Rig 1 ~ (no. 397-556) (180 nos.@ 3nos./d)(CE 041) | P2-Cal.C | 60 | 36 | 18-Sep-17 A | 01-Dec-17 | -204 | 40% | 6 | | | | | | | | |
| LC17664 | Stage 5 -- Preboring for Dia. 2100 Drain Pipe Rig 1 ~ (no. 290-395) (106 nos.@ 3nos./d)(CE 041) | P2-Cal.C | 35 | 35 | 02-Dec-17 | 15-Jan-18 | -204 | 0% | | | | | | | | | |
| LC17664-1 | Footpath diversion and modify water barrier | P2-Cal.C | 21 | 21 | 16-Jan-18 | 08-Feb-18 | -204 | 0% | | | | | | | | | |
| LC17665 | Pipe Pile Installation (165nos. @ 1.5nos./d) | P2-Cal.C | 110 | 110 | 16-Jan-18 | 02-Jun-18 | -183 | 0% | | | | | | | | | |
| Rig 2 | | P2-Cal.C | 36 | 23 | 04-Oct-17 A | 16-Nov-17 | -135 | | 13 | | | | | | | | |
| LC17674-1 | Stage 2 Preboring along Existing EVA to BMPC Rig 2 ~ (no.1061-1084) (23 nos.@ 3nos./d)(CE 041)(CE057) | P2-Cal.C | 8 | 8 | 20-Oct-17 | 30-Oct-17 | -135 | 0% | | | | | | | | | |
| LC17675 | Stage 6 Preboring along Existing EVA to BMPC for Dia. 2100 Drain Pipe Rig 2 ~ (no. 244-289) (46 nos.@ 3nos./d) (CE 041) | P2-Cal.C | 15 | 15 | 04-Oct-17 A | 16-Nov-17 | -135 | 0% | 13 | | | | | | | | |
| Rig 3 | | P2-Cal.C | 123 | 123 | 20-Nov-17 | 23-Apr-18 | -174 | | | | | | | | | | |
| LC17677 | Plant Mobilization (Rig 3) After Chung Yeung Festival (NCE010) | P2-Cal.C | 8 | 8 | 20-Nov-17* | 28-Nov-17 | -174 | 0% | | | | | | | | | |
| LC17677-2 | Stage 7 Preboring along Existing EVA to BMPC Rig 3 ~ (no. 757-816) (60 nos.@ 1.5nos./d) (CE 041) | P2-Cal.C | 40 | 40 | 29-Nov-17 | 17-Jan-18 | -174 | 0% | | | | | | | | | |

— Primary Baseline — Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Oct-17)

3 Months Rolling Programme
 (20 October 2017)
 Page: 8 of 11

| Date | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 20-Oct-17 | | | |

| Activity ID | Activity Name | Calendar | Original Duration | Remaining Duration | Start | Finish | Total Float | Activity % Complete | Variance - BL1 Finish Date | TRA | 2017 | | | | | 2018 | | | |
|--|--|----------|-------------------|--------------------|-------------|-----------|-------------|---------------------|----------------------------|-----|------|-----|-----|-----|-----|------|--|--|--|
| | | | | | | | | | | | Oct | Nov | Dec | Jan | Feb | Jan | Feb | | |
| LC17677-3 | Stage 9 Preboring along Existing EVA to BMCPC Rig 3 ~ (no.825-936) (112 nos.@ 1.5nos./d) (CE 041) | P2-Cal.C | 75 | 75 | 18-Jan-18 | 23-Apr-18 | -174 | 0% | | 0 | | | | | | | | | |
| ELS | | | | | | | | | | | | | | | | | | | |
| SMH 9103-9107 | | P2-Cal.C | 85 | 85 | 17-Aug-17 A | 31-Jan-18 | -67 | | | 0 | | | | | | | ELS | | |
| LC17679 | Sheet Pile installation 24m length (MH9103-9104) (83 nos.@7.5pcs./d) | P2-Cal.C | 12 | 12 | 18-Jan-18 | 31-Jan-18 | -67 | 0% | | 0 | | | | | | | SMH 9103-9107 | | |
| LC17680 | Sheet Pile installation 12m length (MH9104-9105) (180 nos.@15pcs./d) | P2-Cal.C | 12 | 12 | 20-Oct-17 | 03-Nov-17 | -30 | 0% | | 0 | | | | | | | Sheet Pile inst | | |
| LC17682 | Sheet Pile installation 12m length (MH9105-9106) (180nos.@15pcs./d) | P2-Cal.C | 12 | 12 | 13-Nov-17 | 25-Nov-17 | -37 | 0% | | 0 | | | | | | | Sheet Pile installation 12m length (MH9105-9106) (180nos.@15pcs | | |
| LC17684 | Sheet Pile installation 12m length (MH9106-9107) (180 nos.@15pcs./d) | P2-Cal.C | 12 | 12 | 17-Aug-17 A | 15-Dec-17 | -42 | 0% | | 4 | | | | | | | Sheet Pile installation 12m length (MH9106-9107) (180nos.@15pcs | | |
| SMH 9107-9109 | | | | | | | | | | | | | | | | | | | |
| LC17688 | Sheet Pile installation 12m length (SMH9108-9109) (46 nos.@15pcs./d) | P2-Cal.C | 4 | 4 | 16-Jan-18 | 19-Jan-18 | -105 | 0% | | 0 | | | | | | | SMH 9107-9109 | | |
| SMH 9109 - Outfall | | | | | | | | | | | | | | | | | | | |
| LC17699 | Sheet Pile installation 12m length (MH9109-9110) (123 nos.@ 15 nos./d) | P2-Cal.C | 9 | 7 | 18-Oct-17 A | 27-Oct-17 | -17 | 22.22% | | 2 | | | | | | | Sheet Pile installation 12m length (MH9109-9110) (123 nos.@ 15 nos./d) | | |
| New Reclaimed Section | | | | | | | | | | | | | | | | | | | |
| Marine Works | | | 535 | 382 | 20-May-17 A | 05-Nov-18 | 71 | | | 0 | | | | | | | | | |
| Initial Works | | | | | | | | | | | | | | | | | | | |
| MC10156 | Installation of Type 2 Settlement Marker (Type RA) | P2-Cal.C | 7 | 7 | 06-Nov-17 | 13-Nov-17 | -41 | 0% | | 0 | | | | | | | Initial Works | | |
| MC10160 | Baseline for Type 2 Settlement Marker (Type RA) | P2-Cal.C | 3 | 3 | 14-Nov-17 | 16-Nov-17 | -41 | 0% | | 0 | | | | | | | Baseline for Type 2 Settlement Marker (Type RA) | | |
| Steel Cofferdam and Water Gate | | | | | | | | | | | | | | | | | | | |
| Steel Cofferdam Installation | | | | | | | | | | | | | | | | | | | |
| Reinstatement works | | | | | | | | | | | | | | | | | | | |
| Type 1 | | | | | | | | | | | | | | | | | | | |
| I Beam and Sheet Pile Extension | | | | | | | | | | | | | | | | | | | |
| 914 I Beam (2nd Stage) | | P2-Cal.C | 14 | 14 | 03-Oct-17 A | 06-Nov-17 | -226 | | | 0 | | | | | | | I Beam and Sheet Pile Extension | | |
| MC10296-2 | Extension of 914 I Beam (2nd Stage - 8 Joints for Type 1B) | P2-Cal.C | 8 | 4 | 03-Oct-17 A | 24-Oct-17 | -226 | 50% | | 4 | | | | | | | 914 I Beam (2nd Stage) | | |
| MC10296-3 | Extension of 914 I Beam (2nd Stage - 10 Joints for Type 1 Inner Side) | P2-Cal.C | 10 | 10 | 25-Oct-17 | 06-Nov-17 | -226 | 0% | | 0 | | | | | | | Extension of 914 I Beam (2nd Stage - 8 Joints for Type 1B) | | |
| Removal of S/P at transition zone | | | | | | | | | | | | | | | | | | | |
| MC10304-02 | Removal of Underwater S/P | P2-Cal.C | 60 | 60 | 20-Oct-17 | 02-Jan-18 | 307 | 0% | | 0 | | | | | | | Extension of 914 I Beam (2nd Stage - 10 Joints for Type 1 Inner Side) | | |
| Installation | | | | | | | | | | | | | | | | | | | |
| Type 1 | | | | | | | | | | | | | | | | | | | |
| S/P | | | | | | | | | | | | | | | | | | | |
| MC10307-4 | (Barge 1) Installation of Sheet Pile (5th 150 pcs.) + (IW 15Oct - 2day) | P2-Cal.C | 16 | 4 | 07-Oct-17 A | 24-Oct-17 | -223 | 75% | | 11 | | | | | | | Removal of S/P at transition zone | | |
| CHS (Inner side 20nos) | | | | | | | | | | | | | | | | | | | |
| MC10308-1 | (Barge 2) Installation of CHS (Inner Side 2nd 8nos.) + (IW 15Oct - 2day) | P2-Cal.C | 6 | 3 | 22-Sep-17 A | 23-Oct-17 | -225 | 50% | | -19 | | | | | | | Installation | | |
| MC10308-2 | (Barge 2) Installation of CHS (Inner Side 3rd 10nos.) | P2-Cal.C | 5 | 5 | 24-Oct-17 | 30-Oct-17 | -225 | 0% | | 0 | | | | | | | Type 1 | | |
| Guide Beam (Inner Side) | | | | | | | | | | | | | | | | | | | |
| MC10309 | (Barge 2) Installation of Guide Beam (1st 1no) | P2-Cal.C | 1 | 1 | 24-Oct-17 | 24-Oct-17 | -223 | 0% | | 0 | | | | | | | S/P | | |
| MC10309-1 | (Barge 2) Installation of Guide Beam (2nd 4no) | P2-Cal.C | 2 | 2 | 25-Oct-17 | 26-Oct-17 | -223 | 0% | | 0 | | | | | | | (Barge 1) Installation of Sheet Pile (5th 150 pcs.) + (IW 15Oct - 2day) | | |
| MC10309-2 | (Barge 2) Installation of Guide Beam (3rd 5no) | P2-Cal.C | 3 | 3 | 31-Oct-17 | 02-Nov-17 | -225 | 0% | | 0 | | | | | | | CHS (inner side 20nos) | | |
| Type 1A | | | | | | | | | | | | | | | | | | | |
| Guide Beam (Outer Side) | | | | | | | | | | | | | | | | | | | |
| MC10316-4 | Connection of S/P and tie beam stage 2 + (IW 15Oct - 2day) | P2-Cal.C | 30 | 6 | 20-Sep-17 A | 26-Oct-17 | -227 | 80% | | 27 | | | | | | | (Barge 2) Installation of CHS (Inner Side 2nd 8nos.) + (IW 15Oct - 2day) | | |
| Rockfill | | | | | | | | | | | | | | | | | | | |
| MC10319-1 | (Barge 3) RockFill (10m x 2m x 100m) Stage 2 | P2-Cal.C | 4 | 4 | 27-Oct-17 | 01-Nov-17 | -227 | 0% | | 0 | | | | | | | (Barge 2) Installation of CHS (Inner Side 3rd 10nos.) | | |
| Type 1B | | | | | | | | | | | | | | | | | | | |
| CHS (Outer side) | | | | | | | | | | | | | | | | | | | |
| MC10321 | (Barge 2) Installation of CHS (1st batch 9 nos) + (CE069)(CE070)(IW-Sep)(Incl. 9 days inclement Weather)+IW 15Oct -2days | P2-Cal.C | 16 | 2 | 17-Aug-17 A | 21-Oct-17 | -226 | 87.5% | | -7 | | | | | | | Guide Beam (Inner Side) | | |
| Guide Beam (Outer Side) | | | | | | | | | | | | | | | | | | | |
| MC10322-2 | (Barge 2) Reinstatement of Type 1B S/P (75nos) + (IW 15Oct - 2day) | P2-Cal.C | 10 | 1 | 18-Sep-17 A | 23-Oct-17 | -226 | 90% | | -10 | | | | | | | (Barge 2) Installation of Guide Beam (1st 1no) | | |


— Primary Baseline — Critical Remaining Work
— Actual Work ◆ Milestone
— Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Oct-17)

3 Months Rolling Programme
 (20 October 2017)
 Page: 9 of 11

| Date | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 20-Oct-17 | | | |

| Activity ID | Activity Name | Calendar | Original Duration | Remaining Duration | Start | Finish | Total Float | Activity % Complete | Variance - BL1 Finish Date | TRA | 2017 | | | | 2018 | |
|-------------|---|----------|-------------------|--------------------|-------------|-----------|-------------|---------------------|----------------------------|-----|------|-----|-----|-----|------|--|
| | | | | | | | | | | | Oct | Nov | Dec | Jan | Feb | |
| MC10322-4 | Connection of S/P and Tie Beam Stage 2 | P2-Cal.C | 15 | 9 | 20-Oct-17 A | 02-Nov-17 | -223 | 40% | | 6 | | | | | | |
| | Guide Beam (Inner Side) | P2-Cal.C | 2 | 2 | 25-Oct-17 | 26-Oct-17 | -227 | | | 0 | | | | | | |
| MC10324 | Installation of Guide Beam (Barge 3) (2nos.) | P2-Cal.C | 1 | 1 | 25-Oct-17 | 25-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10324-1 | Installation of Guide Beam (Barge 3) (2nos.) | P2-Cal.C | 1 | 1 | 26-Oct-17 | 26-Oct-17 | -227 | 0% | | 0 | | | | | | |
| | Rockfill | P2-Cal.C | 4 | 4 | 27-Oct-17 | 01-Nov-17 | -227 | | | 0 | | | | | | |
| MC10325 | Rockfill (Barge 3) (10m x 2m x 100m) (Stage 1) | P2-Cal.C | 4 | 4 | 27-Oct-17 | 01-Nov-17 | -227 | 0% | | 0 | | | | | | |
| MC10325-0 | Rockfill (Barge 4) (10m x 2m x 100m) (Stage 2) | P2-Cal.C | 4 | 4 | 27-Oct-17 | 01-Nov-17 | -227 | 0% | | 0 | | | | | | |
| | Type 2 | P2-Cal.C | 6 | 6 | 14-Oct-17 A | 27-Oct-17 | -227 | | | 0 | | | | | | |
| | Reinstatement | P2-Cal.C | 6 | 6 | 14-Oct-17 A | 27-Oct-17 | -227 | | | 0 | | | | | | |
| MC10326 | Type 2 reinstatement 2C2 (Barge 3) + (CE069)(CE070) + (IW 15Oct - 2day) | P2-Cal.C | 5 | 1 | 14-Oct-17 A | 21-Oct-17 | -227 | 80% | | 4 | | | | | | |
| MC10326-1 | Type 2 reinstatement 2C1 (Barge 3) + (CE069)(CE070) | P2-Cal.C | 3 | 3 | 23-Oct-17 | 25-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10328-5 | Type 2 re-reinstatement 2B6 & 2A23 (Barge 4) + (CE069)(CE070)(Affect for Typhoon No.8 on 15Oct) | P2-Cal.C | 6 | 3 | 18-Oct-17 A | 24-Oct-17 | -227 | 50% | | 3 | | | | | | |
| MC10328-6 | Type 2 reinstatement 2A24 (Barge 4) + (CE069)(CE070) | P2-Cal.C | 3 | 3 | 25-Oct-17 | 27-Oct-17 | -227 | 0% | | 0 | | | | | | |
| | Type 3 | P2-Cal.C | 53 | 9 | 07-Jul-17 A | 31-Oct-17 | -229 | | | -6 | | | | | | |
| MC10330 | (Barge 2) Connection of Type 3 at Western Portion | P2-Cal.C | 8 | 1 | 07-Jul-17 A | 20-Oct-17 | -229 | 87.5% | | -43 | | | | | | |
| MC10335 | (Barge 4) Connection of Type 3 at Eastern Portion | P2-Cal.C | 8 | 8 | 18-Sep-17 A | 31-Oct-17 | -229 | 0% | | -6 | | | | | | |
| | Water Gate | P2-Cal.C | 35 | 10 | 14-Oct-17 A | 01-Nov-17 | -227 | | | 1 | | | | | | |
| MC10409 | 2nd Stage Loading + (IW 15Oct - 2day) | P2-Cal.C | 8 | 5 | 14-Oct-17 A | 25-Oct-17 | -227 | 37.5% | | -21 | | | | | | |
| MC10410 | S/P Connection at Transition 1A and 1B | P2-Cal.C | 5 | 4 | 18-Oct-17 A | 24-Oct-17 | -227 | 20% | | 1 | | | | | | |
| MC10411 | S/P Surround at Water Gate (W) | P2-Cal.C | 7 | 2 | 18-Oct-17 A | 21-Oct-17 | -227 | 71.43% | | 9 | | | | | | |
| MC10412 | S/P Surround at Water Gate (E) | P2-Cal.C | 9 | 9 | 21-Oct-17 | 01-Nov-17 | -227 | 0% | | 0 | | | | | | |
| | Flexible Joint | P2-Cal.C | 12 | 12 | 20-Oct-17 | 03-Nov-17 | -229 | | | 0 | | | | | | |
| | Installation | P2-Cal.C | 12 | 12 | 20-Oct-17 | 03-Nov-17 | -229 | | | 0 | | | | | | |
| MC10475 | B5B6 | P2-Cal.C | 1 | 1 | 20-Oct-17 | 20-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10476 | A16A17 | P2-Cal.C | 1 | 1 | 20-Oct-17 | 20-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10477 | A17A18 | P2-Cal.C | 1 | 1 | 20-Oct-17 | 20-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10478 | A15A16 | P2-Cal.C | 1 | 1 | 20-Oct-17 | 20-Oct-17 | -226 | 0% | | 0 | | | | | | |
| MC10479 | A14A15 | P2-Cal.C | 1 | 1 | 21-Oct-17 | 21-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10480 | A13A14 | P2-Cal.C | 1 | 1 | 21-Oct-17 | 21-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10481 | A12A13 | P2-Cal.C | 1 | 1 | 21-Oct-17 | 21-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10482 | A11A12 | P2-Cal.C | 1 | 1 | 21-Oct-17 | 21-Oct-17 | -226 | 0% | | 0 | | | | | | |
| MC10483 | A10A11 | P2-Cal.C | 1 | 1 | 23-Oct-17 | 23-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10484 | A9A10 | P2-Cal.C | 1 | 1 | 23-Oct-17 | 23-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10485 | A4A5 | P2-Cal.C | 1 | 1 | 23-Oct-17 | 23-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10486 | A5A6 | P2-Cal.C | 1 | 1 | 23-Oct-17 | 23-Oct-17 | -226 | 0% | | 0 | | | | | | |
| MC10487 | A6A7 | P2-Cal.C | 1 | 1 | 24-Oct-17 | 24-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10488 | A7A8 | P2-Cal.C | 1 | 1 | 24-Oct-17 | 24-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10489 | A8A9 | P2-Cal.C | 1 | 1 | 24-Oct-17 | 24-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10490 | A3A4 | P2-Cal.C | 1 | 1 | 24-Oct-17 | 24-Oct-17 | -226 | 0% | | 0 | | | | | | |
| MC10491 | A2A3 | P2-Cal.C | 1 | 1 | 25-Oct-17 | 25-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10492 | A1A2 | P2-Cal.C | 1 | 1 | 25-Oct-17 | 25-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10493 | A24A1 | P2-Cal.C | 1 | 1 | 25-Oct-17 | 25-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10494 | A23A24 | P2-Cal.C | 1 | 1 | 25-Oct-17 | 25-Oct-17 | -226 | 0% | | 0 | | | | | | |
| MC10495 | B6A23 | P2-Cal.C | 1 | 1 | 26-Oct-17 | 26-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10496 | C1C2 | P2-Cal.C | 1 | 1 | 26-Oct-17 | 26-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10497 | 2C1Type 1 | P2-Cal.C | 1 | 1 | 26-Oct-17 | 26-Oct-17 | -227 | 0% | | 0 | | | | | | |
| MC10498 | South Water Gate | P2-Cal.C | 1 | 1 | 26-Oct-17 | 26-Oct-17 | -226 | 0% | | 0 | | | | | | |

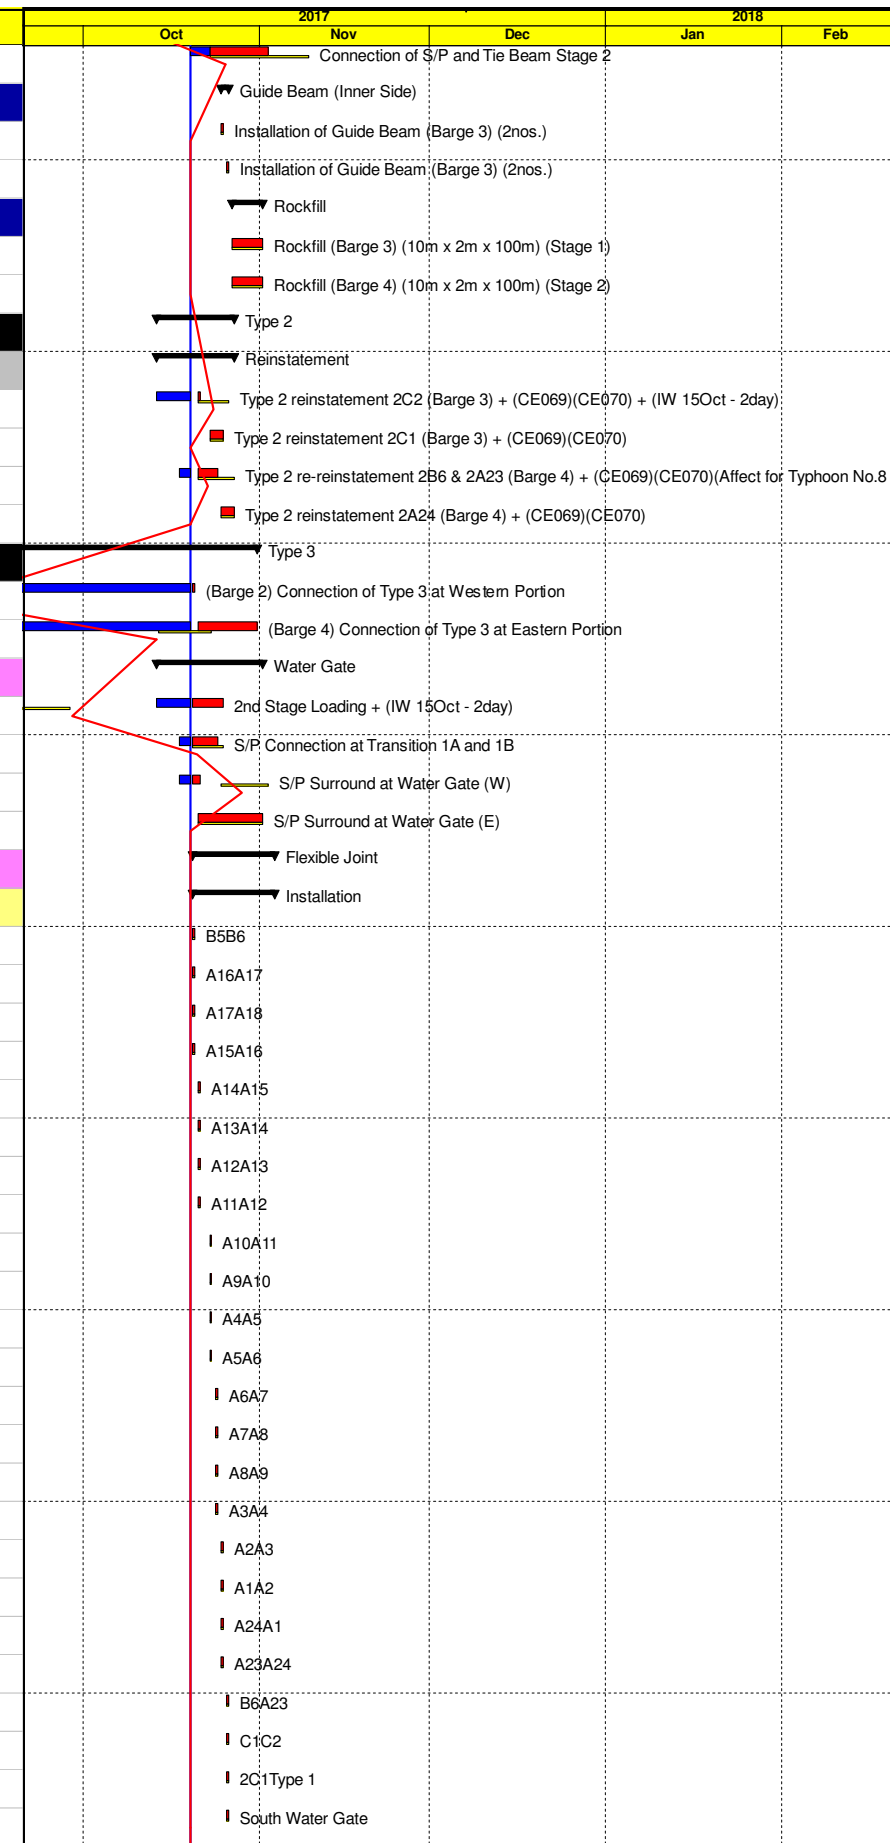

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Oct-17)

3 Months Rolling Programme
 (20 October 2017)
 Page: 10 of 11

| | | | |
|-----------|----------|---------|----------|
| Date | Revision | Checked | Approved |
| 20-Oct-17 | | | |

| Activity ID | Activity Name | Calendar | Original Duration | Remaining Duration | Start | Finish | Total Float | Activity % Complete | Variance - BL1 | TRA | 2017 | | | | | 2018 | |
|---|--|----------|-------------------|--------------------|-------------|------------|-------------|---------------------|----------------|-----|------|-----|-----|-----|-----|------|-----|
| | | | | | | | | | | | Oct | Nov | Dec | Jan | Feb | Jan | Feb |
| MC10498-1 | North Water Gate | P2-Cal.C | 1 | 1 | 27-Oct-17 | 27-Oct-17 | -227 | 0% | | | | | | | | | |
| MC10498-2 | 2D3Type 1B | P2-Cal.C | 1 | 1 | 27-Oct-17 | 27-Oct-17 | -227 | 0% | | | | | | | | | |
| MC10499 | Trial Operation of Circulation Pump | P2-Cal.C | 3 | 3 | 01-Nov-17 | 03-Nov-17 | -229 | 0% | | | | | | | | | |
| Dredging Work | | P2-Cal.C | 68 | 68 | 04-Nov-17 | 25-Jan-18 | -229 | | | | | | | | | | |
| MC10500 | Dredge CH50-71 (Upper) (1777m3) | P2-Cal.C | 1 | 1 | 04-Nov-17 | 04-Nov-17 | -229 | 0% | | | | | | | | | |
| MC10505 | Dredge CH71-100 (Upper) (7108m3) | P2-Cal.C | 4 | 4 | 06-Nov-17 | 09-Nov-17 | -229 | 0% | | | | | | | | | |
| MC10515 | Dredge CH100-150 (Upper) (17770m3) | P2-Cal.C | 10 | 10 | 10-Nov-17 | 21-Nov-17 | -229 | 0% | | | | | | | | | |
| MC10525 | Dredge CH150-200 (Upper) (23101m3) | P2-Cal.C | 13 | 13 | 22-Nov-17 | 06-Dec-17 | -229 | 0% | | | | | | | | | |
| MC10535 | Dredge CH50-71 (Bottom) (1109m3) | P2-Cal.C | 1 | 1 | 07-Dec-17 | 07-Dec-17 | -229 | 0% | | | | | | | | | |
| MC10555 | Dredge CH71-100 (Bottom) (2725m3) | P2-Cal.C | 2 | 2 | 08-Dec-17 | 09-Dec-17 | -229 | 0% | | | | | | | | | |
| MC10575 | Dredge CH100-150 (Bottom) (4944m3) | P2-Cal.C | 3 | 3 | 11-Dec-17 | 13-Dec-17 | -229 | 0% | | | | | | | | | |
| MC10595 | Dredge CH200-250 (Upper) (26655m3) | P2-Cal.C | 15 | 15 | 14-Dec-17 | 03-Jan-18 | -229 | 0% | | | | | | | | | |
| MC10615 | Dredge CH150-200 (Bottom) (4672m3) | P2-Cal.C | 3 | 3 | 04-Jan-18 | 06-Jan-18 | -229 | 0% | | | | | | | | | |
| MC10635 | Dredge CH250-300 (Upper) (28432m3) | P2-Cal.C | 16 | 16 | 08-Jan-18 | 25-Jan-18 | -229 | 0% | | | | | | | | | |
| Bathymetric and Seismic Survey | | P2-Cal.C | 23 | 23 | 11-Dec-17 | 09-Jan-18 | -205 | | | | | | | | | | |
| MC10875 | Survey CH50-100 | P2-Cal.C | 2 | 2 | 11-Dec-17 | 12-Dec-17 | -204 | 0% | | | | | | | | | |
| MC10895 | Survey CH100-150 | P2-Cal.C | 2 | 2 | 14-Dec-17 | 15-Dec-17 | -205 | 0% | | | | | | | | | |
| MC10915 | Survey CH150-200 | P2-Cal.C | 2 | 2 | 08-Jan-18 | 09-Jan-18 | -205 | 0% | | | | | | | | | |
| Filling of Recycle G400 Rock at Dredged Trench | | P2-Cal.C | 18 | 18 | 27-Dec-17 | 17-Jan-18 | -205 | | | | | | | | | | |
| MC11055 | Fill of Recycle G400 at CH60-112 (7237m3) | P2-Cal.C | 4 | 4 | 27-Dec-17 | 30-Dec-17 | -212 | 0% | | | | | | | | | |
| MC11085 | Fill Recycle G400 at CH112-162 (12707m3) | P2-Cal.C | 7 | 7 | 10-Jan-18 | 17-Jan-18 | -205 | 0% | | | | | | | | | |
| Construction of Eastern Seawall (Dredged Area) | | P2-Cal.C | 18 | 18 | 02-Jan-18 | 22-Jan-18 | -194 | | | | | | | | | | |
| Laying of Geotextile Type A (Trench) | | P2-Cal.C | 15 | 15 | 02-Jan-18 | 18-Jan-18 | -194 | | | | | | | | | | |
| MC11325 | Geotextile Type A CH60-112 (801m2) | P2-Cal.C | 1 | 1 | 02-Jan-18 | 02-Jan-18 | -212 | 0% | | | | | | | | | |
| MC11335 | Geotextile Type A CH112-162 (889m2) | P2-Cal.C | 1 | 1 | 18-Jan-18 | 18-Jan-18 | -194 | 0% | | | | | | | | | |
| Laying of Granular Filter (Trench) | | P2-Cal.C | 17 | 17 | 03-Jan-18 | 22-Jan-18 | -194 | | | | | | | | | | |
| MC11415 | Granular Filter CH60-112 (1382m3) | P2-Cal.C | 2 | 2 | 03-Jan-18 | 04-Jan-18 | -212 | 0% | | | | | | | | | |
| MC11425 | Granular Filter CH112-162 (2051m3) | P2-Cal.C | 3 | 3 | 19-Jan-18 | 22-Jan-18 | -194 | 0% | | | | | | | | | |
| Laying Geotextile Type A | | P2-Cal.C | 5 | 5 | 05-Jan-18 | 10-Jan-18 | -212 | | | | | | | | | | |
| MC12005 | Geotextile Type A (No-Dredged Area) CH0-112 (4369m2) | P2-Cal.C | 5 | 5 | 05-Jan-18 | 10-Jan-18 | -212 | 0% | | | | | | | | | |
| Placing Sand Blanket (Non-Dredged Area) | | P2-Cal.C | 8 | 8 | 11-Jan-18 | 19-Jan-18 | -212 | | | | | | | | | | |
| MC12095 | Sand Blanket CH0-100 (3527m3) | P2-Cal.C | 8 | 8 | 11-Jan-18 | 19-Jan-18 | -212 | 0% | | | | | | | | | |
| Full-scale Treatment of Cement S/S of Marine Sediment | | | 535 | 382 | 20-May-17 A | 05-Nov-18 | -38 | | | | | | | | | | |
| MC14015 | Loading and unloading Point | P2-Cal.C | 34 | 37 | 20-May-17 A | 02-Dec-17 | -8 | 0% | -130 | | | | | | | | |
| MC14020 | Delivery of concrete block | P2-Cal.A | 0 | 0 | | 20-Oct-17* | -24 | 0% | | | | | | | | | |
| MC14035 | Set up of Curing Area | P2-Cal.C | 48 | 48 | 03-Nov-17 | 30-Dec-17 | -30 | 0% | | | | | | | | | |
| MC14055 | Set up Cement S/S Treatment Facility | P2-Cal.C | 48 | 48 | 03-Nov-17 | 30-Dec-17 | -30 | 0% | | | | | | | | | |
| MC14075 | Treatment | P2-Cal.C | 250 | 250 | 02-Jan-18 | 05-Nov-18 | -30 | 0% | | | | | | | | | |
| Section 4 of the Works - Preservation and Protection of Existing Trees | | P2-Cal.A | 1451 | 1356 | 12-Jan-17 A | 06-Jul-21 | -283 | | | | | | | | | | |
| LC25260 | Preservation and Protection of Existing Trees | P2-Cal.A | 1451 | 1356 | 12-Jan-17 A | 06-Jul-21 | -283 | 6.55% | -186 | | | | | | | | |
| Section 5 of the Works - Landscaping Works | | P2-Cal.C | 182 | 79 | 12-Jan-17 A | 24-Jan-18 | -187 | | | | | | | | | | |
| LC25320 | Tree Transplanting Preparation Works | P2-Cal.C | 182 | 79 | 12-Jan-17 A | 24-Jan-18 | -187 | 56.59% | -125 | | | | | | | | |

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Oct-17)

3 Months Rolling Programme
 (20 October 2017)
 Page: 11 of 11

| Date | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 20-Oct-17 | | | |

Subject: 3 Months Look Ahead Programme


| Activities | Nov, 2017 | | Dec, 2017 | | Jan, 2017 | |
|----------------------------------|-----------|--|-----------|--|-----------|--|
| Construction of retaining Wal | | | | | | |
| Piling Construction at East Pier | | | | | | |
| Construction of footing - 1& 2 | | | | | | |

**APPENDIX R
RECORD OF LANDFILL GAS
MONITORING BY CONTRACTOR**


APPENDIX R - RECORD OF LANDFILL GAS MONITORING BY THE CONTRACTOR

| Location | Date of Measurement | Sampling time | Weather Condition | Temperature (°C) | Methane (%) | Carbon dioxide (%) | Oxygen (%) |
|-------------|---------------------|---------------|-------------------|------------------|-------------|--------------------|------------|
| Portion III | 3-Oct-17 | 08:30 | Cloudy | 28 | 0 | 0 | 20.9 |
| | 3-Oct-17 | 13:01 | Cloudy | 31 | 0 | 0 | 20.9 |
| | 4-Oct-17 | 08:31 | Rainy | 30 | 0 | 0 | 20.9 |
| | 4-Oct-17 | 13:00 | Rainy | 32 | 0 | 0 | 20.9 |
| | 6-Oct-17 | 08:28 | Cloudy | 29 | 0 | 0 | 20.9 |
| | 6-Oct-17 | 13:03 | Cloudy | 33 | 0 | 0 | 20.9 |
| | 7-Oct-17 | 08:28 | Sunny | 30 | 0 | 0 | 20.9 |
| | 7-Oct-17 | 13:02 | Sunny | 33 | 0 | 0 | 20.9 |
| | 9-Oct-17 | 08:30 | Cloudy | 27 | 0 | 0 | 20.9 |
| | 9-Oct-17 | 13:03 | Cloudy | 30 | 0 | 0 | 20.9 |
| | 10-Oct-17 | 08:30 | Rainy | 28 | 0 | 0 | 20.9 |
| | 10-Oct-17 | 13:02 | Cloudy | 32 | 0 | 0 | 20.9 |
| | 11-Oct-17 | 08:30 | Cloudy | 29 | 0 | 0 | 20.9 |
| | 11-Oct-17 | 13:05 | Cloudy | 33 | 0 | 0 | 20.9 |
| | 12-Oct-17 | 08:30 | Sunny | 29 | 0 | 0 | 20.9 |
| | 12-Oct-17 | 13:02 | Sunny | 33 | 0 | 0 | 20.9 |
| | 13-Oct-17 | 08:30 | Sunny | 27 | 0 | 0 | 20.9 |
| | 13-Oct-17 | 13:00 | Sunny | 30 | 0 | 0 | 20.9 |
| | 14-Oct-17 | 08:30 | Cloudy | 24 | 0 | 0 | 20.9 |
| | 14-Oct-17 | 13:03 | Rainy | 29 | 0 | 0 | 20.9 |
| | 16-Oct-17 | 08:30 | Rainy | 24 | 0 | 0 | 20.9 |
| | 16-Oct-17 | 13:04 | Rainy | 27 | 0 | 0 | 20.9 |
| | 17-Oct-17 | 08:30 | Rainy | 24 | 0 | 0 | 20.9 |
| | 17-Oct-17 | 13:03 | Rainy | 26 | 0 | 0 | 20.9 |
| | 18-Oct-17 | 08:30 | Cloudy | 28 | 0 | 0 | 20.9 |
| | 18-Oct-17 | 13:03 | Cloudy | 31 | 0 | 0 | 20.9 |
| | 19-Oct-17 | 08:30 | Sunny | 27 | 0 | 0 | 20.9 |
| | 19-Oct-17 | 13:02 | Cloudy | 30 | 0 | 0 | 20.9 |
| | 20-Oct-17 | 08:30 | Sunny | 27 | 0 | 0 | 20.9 |
| | 20-Oct-17 | 13:00 | Sunny | 30 | 0 | 0 | 20.9 |
| | 21-Oct-17 | 08:30 | Sunny | 24 | 0 | 0 | 20.9 |
| 21-Oct-17 | 13:00 | Sunny | 28 | 0 | 0 | 20.9 | |
| 23-Oct-17 | 08:30 | Sunny | 24 | 0 | 0 | 20.9 | |
| 23-Oct-17 | 13:05 | Sunny | 27 | 0 | 0 | 20.9 | |
| 24-Oct-17 | 08:30 | Sunny | 25 | 0 | 0 | 20.9 | |
| 24-Oct-17 | 13:01 | Sunny | 29 | 0 | 0 | 20.9 | |
| 25-Oct-17 | 08:28 | Cloudy | 25 | 0 | 0 | 20.9 | |
| 25-Oct-17 | 13:00 | Rainy | 27 | 0 | 0 | 20.9 | |
| 26-Oct-17 | 08:30 | Cloudy | 23 | 0 | 0 | 20.9 | |
| 26-Oct-17 | 13:07 | Sunny | 26 | 0 | 0 | 20.9 | |
| 27-Oct-17 | 08:30 | Sunny | 25 | 0 | 0 | 20.9 | |
| 27-Oct-17 | 13:05 | Sunny | 29 | 0 | 0 | 20.9 | |
| 30-Oct-17 | 08:27 | Cloudy | 23 | 0 | 0 | 20.9 | |
| 30-Oct-17 | 13:02 | Cloudy | 28 | 0 | 0 | 20.9 | |
| 31-Oct-17 | 08:30 | Cloudy | 26 | 0 | 0 | 20.9 | |
| 31-Oct-17 | 13:05 | Rainy | 28 | 0 | 0 | 20.9 | |


Methane

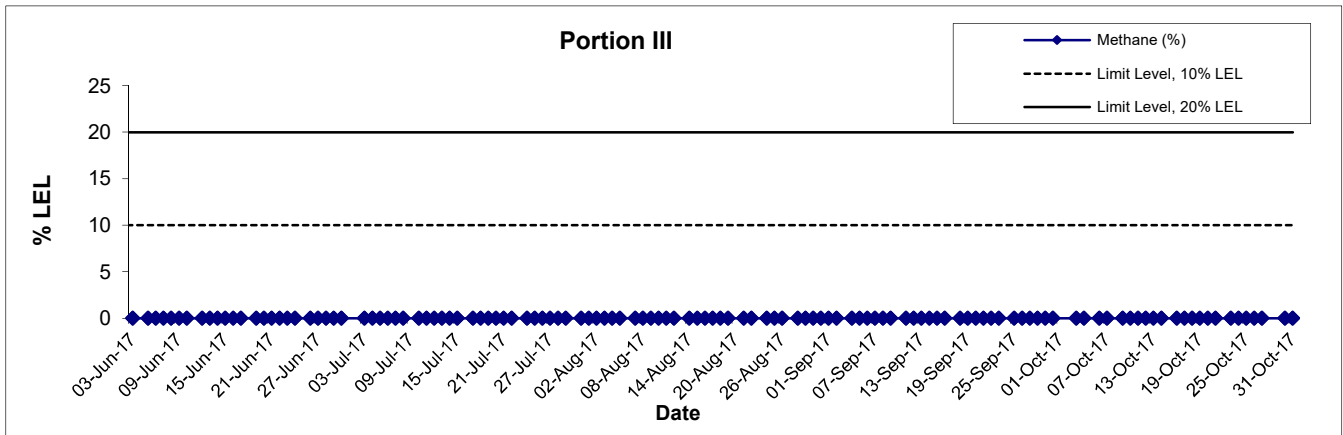


Carbon Dioxide

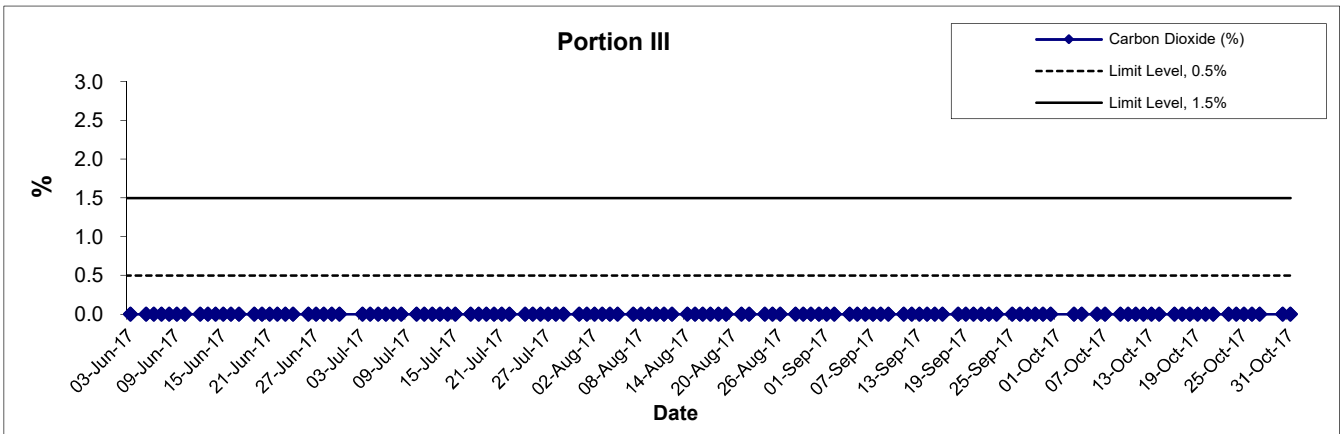

Oxygen

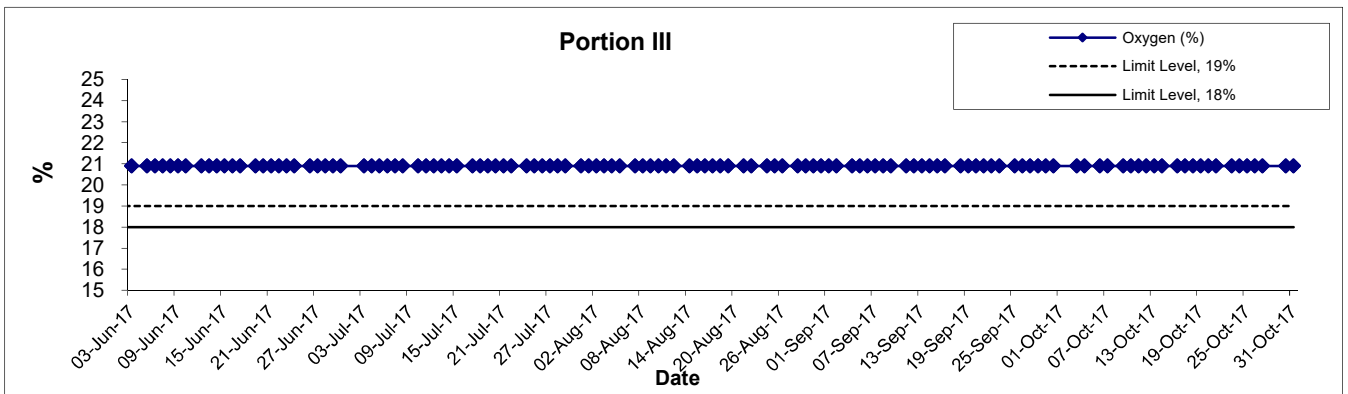

| | | | | |
|-------|---|--------|-------|-------------|
| Title | Agreement No. CE 59/2015 (EP) | | Scale | Project |
| | Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction | | N.T.S | No. MA16034 |
| | Graphical Presentation of Landfill Gas Measurement | | Date | Appendix R |
| | | Sep 17 | | |



**APPENDIX S
UPDATED CONSTRUCTION NOISE
ASSESSMENT**

No update on Construction Noise Assessment in the reporting month

**APPENDIX T
PHOTO RECORD OF POST-
TRANSLOCATION CORAL
MONITORING SURVEY**

No post-translocation coral monitoring was conducted in the reporting month
