


Civil Engineering and Development Department

**Agreement No. CE 59/2015 (EP)
Environmental Team for
Tseung Kwan O – Lam Tin Tunnel
Design and Construction**

**Monthly Environmental Monitoring and
Audit Report for April 2018**

(version 2.0)

Approved By 
(Dr. Priscilla Choy,
Environmental Team Leader)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties.

CINOTECH CONSULTANTS LTD

Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong
Tel: (852) 2151 2083 Fax: (852) 3107 1388
Email: info@cinotech.com.hk

TABLE OF CONTENTS

EXECUTIVE SUMMARY.....	1
Introduction.....	1
Environmental Monitoring Works.....	1
Key Information in the Reporting Month.....	3
Key Construction Work in the reporting month & the next reporting month.....	3
Future Key Issues.....	4
1. INTRODUCTION.....	6
Purpose of the Report.....	6
Structure of the Report.....	6
2. PROJECT INFORMATION.....	8
Background.....	8
Project Organizations.....	8
Construction Activities undertaken during the Reporting Month.....	9
Status of Environmental Licences, Notification and Permits.....	10
Summary of EM&A Requirements.....	12
3. AIR QUALITY.....	13
Monitoring Requirements.....	13
Monitoring Locations.....	13
Monitoring Equipment.....	13
Monitoring Parameters and Frequency.....	14
Monitoring Methodology.....	14
Results and Observations.....	17
4. NOISE.....	18
Monitoring Requirements.....	18
Monitoring Locations.....	18
Monitoring Equipments.....	18
Monitoring Methodology and QA/QC Procedure.....	19
Results and Observations.....	20
Updated Construction Noise Assessment.....	20
5. WATER QUALITY.....	21
Monitoring Requirements.....	21
Monitoring Locations.....	22
Monitoring Equipments.....	22
Monitoring Parameters and Frequency.....	24
Monitoring Methodology.....	25
Laboratory Analytical Methods.....	26
QA/QC Requirements.....	26
Decontamination Procedures.....	26
Sampling Management and Supervision.....	26
Results and Observations.....	26
6. ECOLOGY.....	28
Post-Translocation Coral Monitoring.....	28
Event and Action Plan.....	28

Results and Observations.....	28
7. CULTURAL HERITAGE	29
Monitoring Requirement	29
Monitoring Locations	29
Monitoring Equipment	29
Monitoring Methodology.....	29
Alert, Alarm and Action Levels.....	30
Results	30
Mitigation Measures for Cultural Heritage.....	30
8. LANDSCAPE AND VISUAL IMPACT REQUIREMENTS.....	31
9. LANDFILL GAS MONITORING	32
Monitoring Requirement	32
Monitoring Parameters and Frequency.....	32
Monitoring Locations	32
Monitoring Equipment	32
Results and Observations.....	33
10. ENVIRONMENTAL AUDIT.....	34
Site Audits.....	34
Implementation Status of Environmental Mitigation Measures	34
11. WASTE MANAGEMENT	35
12. ENVIRONMENTAL NON-CONFORMANCE	36
Summary of Exceedances.....	36
Summary of Environmental Non-Compliance	36
Summary of Environmental Complaint.....	36
Summary of Environmental Summon and Successful Prosecution	36
13. FUTURE KEY ISSUES	37
Key Issues for the Coming Month	38
Monitoring Schedule for the Next Month	38
14. CONCLUSIONS AND RECOMMENDATIONS.....	39
Conclusions.....	39
Recommendations	40

LIST OF TABLES

Table I	Non-compliance (exceedance) Recorded for the Project in the Reporting Month
Table II	Summary Table for Key Information in the Reporting Month
Table III	Summary Table for Key Construction Work in the Reporting Month
Table IV	Summary Table for Site Activities in the next Reporting Period
Table 2.1	Key Project Contacts
Table 2.2	Summary Table for Major Site Activities in the Reporting Month
Table 2.3	Construction Programme Showing the Inter-Relationship with Environmental Protection/Mitigation Measures
Table 2.4	Summary of the Status of Environmental Licences, Notification and Permits
Table 3.1	Locations for Air Quality Monitoring
Table 3.2	Air Quality Monitoring Equipment
Table 3.3	Impact Dust Monitoring Parameters, Frequency and Duration
Table 3.4	Major Dust Source during Air Quality Monitoring
Table 4.1	Noise Monitoring Stations
Table 4.2	Noise Monitoring Equipment
Table 4.3	Noise Monitoring Parameters, Frequency and Duration
Table 4.4	Major Noise Source during Noise Monitoring
Table 4.5	Baseline Noise Level and Noise Limit Level for Monitoring Stations
Table 5.1	Groundwater Quality Monitoring Stations
Table 5.2	Marine Water Quality Monitoring Stations
Table 5.3	Water Quality Monitoring Equipment
Table 5.4	Water Quality Monitoring Parameters and Frequency
Table 5.5	Methods for Laboratory Analysis for Water Samples
Table 5.6	Summary of Groundwater Quality Monitoring Results
Table 6.1	Location and Physical attributes of the Coral Recipient Site
Table 7.1	Cultural Heritage Monitoring Equipment
Table 7.2	AAA Levels for Monitoring for Cultural Heritage
Table 9.1	Landfill Gas Monitoring Equipment
Table 13.1	Summary Table for Site Activities in the next Reporting Period

LIST OF FIGURES

Figure 1	Site Layout Plan
Figure 1a	Site Portions under Works Contract No. NE/2015/01 (Lam Tin Side)
Figure 1b	Site Portions under Works Contract No. NE/2015/01 (Tseung Kwan O Side)
Figure 1c	Site Portions under Works Contract No. NE/2015/02
Figure 1d	Site Portions under Works Contract No. NE/2015/03
Figure 1e	Site Portions under Works Contract No. NE/2017/01
Figure 1f	Site Portions under Works Contract No. NE/2017/01
Figure 1g	Site Portions under Works Contract No. NE/2017/02
Figure 1h	Site Portions under Works Contract No. NE/2017/02
Figure 2	Locations of Air Quality Monitoring Stations
Figure 3	Locations of Construction Noise Monitoring Stations
Figure 4	Locations of Groundwater Quality Monitoring Stations
Figure 5	Locations of Marine Water Quality Monitoring Stations
Figure 6	Locations of Landfill Gas Monitoring
Figure 7	Location of Post-translocation Coral Monitoring
Figure 8	Location of Monitoring for Cultural Heritage
Figure 9	Location of Water Quality Monitoring in Temporary Embayment

LIST OF APPENDICES

Appendix A	Action and Limit Levels
Appendix B	Copies of Calibration Certificates
Appendix C	Weather Information
Appendix D	Environmental Monitoring Schedules
Appendix E	1-hour TSP Monitoring Results and Graphical Presentations
Appendix F	24-hour TSP Monitoring Results and Graphical Presentations
Appendix G	Noise Monitoring Results and Graphical Presentations
Appendix H	Groundwater Quality Monitoring Results, Graphical Presentations and Laboratory Testing Reports
Appendix I	Marine Water Quality Monitoring Results and Graphical Presentations
Appendix J	Quality Control Reports for Laboratory Analysis
Appendix K	Summary of Exceedance
Appendix L	Site Audit Summary
Appendix M	Event and Action Plans
Appendix N	Implementation Schedule And Recommended Mitigation Measures
Appendix O	Summaries of Environmental Complaint, Warning, Summon and Notification of Successful Prosecution
Appendix P	Waste Generation in the Reporting Month
Appendix Q	Tentative Construction Programme
Appendix R	Record of Landfill Gas Monitoring by Contractor
Appendix S	Updated Construction Noise Assessment
Appendix T	Cultural Heritage Monitoring Results

EXECUTIVE SUMMARY**Introduction**

1. This is the 18th Environmental Monitoring and Audit (EM&A) Report prepared by Cinotech Consultants Limited for the “Agreement No. CE 59/2015 (EP) Environmental Team for Tseung Kwan O – Lam Tin Tunnel – Design and Construction” (hereinafter called “the Project”). This report documents the findings of EM&A Works conducted in April 2018.
2. During the reporting month, the following works contracts were undertaken:
 - Contract No. NE/2015/01 – Tseung Kwan O – Lam Tin Tunnel – Main Tunnel and Associated Works;
 - Contract No. NE/2015/02 – Tseung Kwan O – Lam Tin Tunnel – Road P2 and Associated Works;
 - Contract No. NE/2015/03 – Tseung Kwan O – Lam Tin Tunnel – Northern Footbridge;
 - Contract No. NE/2017/01 – Tseung Kwan O – Lam Tin Tunnel –Tseung Kwan O Interchange and Associated Works
 - Contract No. NE/2017/02 – Tseung Kwan O – Lam Tin Tunnel – Road P2/D4 and Associated Works.

Environmental Monitoring Works

3. Environmental monitoring for the Project was performed in accordance with the EM&A Manual and the monitoring results were checked and reviewed. Site Inspections/Audits were conducted once per week. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.
4. Summary of the non-compliance (exceedance) in the reporting month for the Project is tabulated in **Table I**.

Table I Non-compliance (exceedance) Record for the Project in the Reporting Month

Environmental Monitoring	No. of Non-compliance (Exceedance)		No. of Non-compliance (Exceedance) due to Construction Activities of this Project		Action Taken
	Action Level	Limit Level	Action Level	Limit Level	
Air Quality	0	0	0	0	N/A
Noise	13	0	0(*)	0	Refer to Appendix O
Groundwater Quality	1	12	0(*)	0(*)	N/A
Marine Water Quality	0	0	0	0	N/A
Groundwater Level Monitoring (Piezometer Monitoring)	N/A	N/A	N/A	N/A	N/A
Ecological	N/A	N/A	N/A	N/A	N/A
Cultural Heritage	0	0	0	0	N/A
Landfill Gas	0	0	0	0	N/A

Note (*): Environmental complaints received from April 2018 and the exceedance for groundwater quality recorded on 24 April 2018 are still under investigation.

*Action Taken by the Contractor after received the complaint (Details of the complaints are shown in **Appendix O**)*

- Portable generator was enclosed by an acoustic enclosure;
- Vibratory roller was operated with an acoustic baffle;
- Immediately cleaned the dust and dirt on Tong Yin Street and Chi Shin Street;
- Additional notice would be set up to remind the truck driver to perform wheel washing properly before leaving site;
- Noise sources on the barge and dredger were covered with acoustic materials.
- To improve performance by dump truck drivers, training has been provided by the Contractor to all staffs and dump truck drivers.

Air Quality Monitoring

5. All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
6. All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

Construction Noise Monitoring

7. All noise monitoring was conducted as scheduled in the reporting month. Thirteen (13) Action Level exceedance was recorded due to the documented complaints received in this reporting month. No Limit Level exceedance was recorded in the reporting month.

Water Quality Monitoring

8. Groundwater monitoring was conducted as scheduled in the reporting month. One Action Level and Twelve Limit Level exceedances were recorded in the reporting.
9. All marine water monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
10. Construction phase daily piezometer monitoring was not carried out in this reporting period as there is no tunnel construction activities are carried out within +/- 50m of the piezometer gate in plan.

Ecological Monitoring

11. Post-translocation coral monitoring survey shall be conducted once every 3 months for a period of 12 months after completion of coral translocation. The post-translocation coral monitoring surveys were completed in November 2017.

Monitoring on Cultural Heritage

12. Monitoring of impacts on Cultural Heritage at Cha Kwo Ling Tin Hau Temple commenced in April 2017. No Alert Alarm and Action (AAA) Level exceedance was recorded in the reporting month.

Landscape and Visual Monitoring and Audit

13. The implementation of landscape and visual mitigation measures was checked during the environmental site inspections. Recommended follow-up actions have been discharged by the Contractor. Details of the audit findings and implementation status are presented in Section 10.

Landfill Gas Monitoring

14. Monitoring of landfill gases commenced in December 2016 and were carried out by the Contractor at excavation location, Portion III. No Limit Level exceedance was recorded.

Environmental Site Inspection

15. Joint weekly site inspections were conducted by representatives of the Contractor, Engineer and Environmental Team. The representative of the IEC joined the site inspection for NE/2015/01, NE/2015/02, NE/2015/03, NE/2017/01 and NE/2017/02 on 25, 26, 11, 24, 16 April 2018 respectively. Details of the audit findings and implementation status are presented in Section 10.

Waste Management

16. Wastes generated from this Project include inert construction and demolition (C&D) materials, non-inert C&D materials and marine sediments. Details of waste management data is presented in Section 11 and **Appendix P**.

Key Information in the Reporting Month

17. Summary of key information in the reporting month is tabulated in **Table II**.

Table II Summary Table for Key Information in the Reporting Month

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Complaint received by Project Team / Complaint referred by EPD (April 2018)	14	Noise nuisance / Light pollution / Odour nuisance	Under investigation	On-going	Details refer to App O
Complaint received by Project Team / Complaint referred by EPD (March 2018)	17*	Construction dust / noise nuisance / Visual & Landscape	Under investigation	On-going	
Complaint received by Project Team / Complaint referred by EPD (February 2018)	6	Construction dust / noise nuisance	Under investigation	On-going	
Notifications of any summons & prosecutions received	0	---	N/A	N/A	---

Note (*): The number of complaints in March 2018 has been updated.

Key Construction Work in the reporting month & the next reporting month

18. Summary of key construction work in the reporting month is tabulated in **Table III**.

Table III Summary Table for Key Construction Work in the Reporting Month

Contract No.	Project Title	Site Activities (April 2018)
--------------	---------------	------------------------------

NE/2015/01	Tseung Kwan O – Lam Tin Tunnel – Main Tunnel and Associated Works	Lam Tin Interchange	1) EHC2 U-Trough 2) Site Formation – Area 1G1, Area 1G2, Area 2, Area 3, Area 4 & Area 5 3) Pipe Pile wall – Area 2A
		Main Tunnel	1) Main tunnel Excavation
		TKO Interchange	1) Haul Road Construction, Site Formation and Slope Works 2) Steel Platform for Bridge Construction
NE/2015/02	Tseung Kwan O – Lam Tin Tunnel – Road P2 and Associated Works	1) Installation of DN2100 Concrete Pipe at Portion IV & VII 2) ELS Installation for U-Trough at Portion V & VI 3) Construction of Retaining Wall and U-Trough at Portion VIII 4) Enhancement of Temporary Steel Cofferdam at Portion IX 5) Dredging Works and Armour Rock Removal at Portion IX 6) Treatment of Marine Sediment at Area A 7) General Site Clearance and Hoarding Erection	
NE/2015/03	Tseung Kwan O – Lam Tin Tunnel – Northern Footbridge	1) Erection of falsework system	
NE/2017/01	Tseung Kwan O – Lam Tin Tunnel – Tseung Kwan O Interchange and Associated Works	1. Construction of Site Office	
NE/2017/02	Tseung Kwan O – Lam Tin Tunnel – Road P2/D4 and Associated Works	1) Trial pit 2) Underground utilities detection 3) Temporary traffic arrangement Setup 4) Site office erection 5) Communication Liaison Center erection 6) Modification of traffic island 7) Fencing erection	

Future Key Issues

19. The future key environmental issues in the coming month include:

Table IV Summary Table for Site Activities in the next Reporting Period

Contract No. and Project Title	Site Activities (May 2018)		Key environmental issues *
NE/2015/01 - Tseung Kwan O – Lam Tin Tunnel – Main Tunnel and Associated Works	Lam Tin Interchange	1) EHC2 U-Trough 2) Site Formation – Area 1G1, Area 1G2, Area 2, Area 3, Area 4 & Area 5	(A)/ (B) / (C) / (D) / (E) (G)
	Main Tunnel	1) Main Tunnel Excavation	(B)

	TKO Interchange	1) Haul Road Construction and Site Formation & Slope Works 2) Steel Platform for Bridge Construction	(A) / (C) / (D) / (E) / (F) / (I)
NE/2015/02 - Tseung Kwan O – Lam Tin Tunnel – Road P2 and Associated Works		1) Pre-bored works, sheet piling and interlocking pipe piles installation works at Portion IV & VII 2) Removal of existing seawall blocks at Portion IV & VII 3) Reconstruction of existing outfall and installation of DN2100 drainage system at Portion IV & VII 4) Pre-bored works at Portion V & VI 5) Waterproofing, backfilling works and wall construction at Portion VIII 6) Dredging at Portion IX 7) Seawall Construction at Portion IX 8) Placing sand blanket at non-dredged area at Portion IX	(A) / (B) / (C) / (D) / (E) / (G) / (I)
NE/2015/03 - Tseung Kwan O – Lam Tin Tunnel – Northern Footbridge		1) Construction of Pile Cap PC4 and Sump Pit 2) Install steel mould for main deck	(A) / (B) / (C) / (D) / (E)
NE/2017/01 – Tseung Kwan O Interchange and Associated Works		1) Construction of Site Office 2) Erection of Temporary platform for pre-drill and bore pile work 3) Ground Investigation Works	(A) / (B) / (E) / (F) / (G)
NE/2017/02 – Tseung Kwan O - Lam Tin Tunnel - Road P2/D4 and Associated Works		1) Trial pit 2) Underground utilities detection 3) Temporary traffic arrangement Setup 4) Site office erection 5) Communication Liaison Center erection 6) Modification of traffic island 7) Fencing erection 8) Predrilling 9) Construction of drainage and watermain	(A) / (B) / (E) / (F) / (G)

Note:

- (A) Watering for dust generation from haul road, stockpiles of dusty materials, exposed site area, excavation works and rock breaking activities;
- (B) Noisy construction activity such as rock-breaking activities and piling works;
- (C) Runoff from exposed slope or site area;
- (D) Wastewater and runoff discharge from site;
- (E) Accumulation of silt, mud and sand along U-channels and sedimentation tanks;
- (F) Set up and implementation of temporary drainage system for the surface runoff;
- (G) Storage of chemicals/fuel and chemical waste/waste oil on site;
- (H) Accumulation and storage of general and construction waste on site; and
- (I) Marine water quality impact and indirect impact to coral communities due to marine construction for TKO-LTT reclamation.

1. INTRODUCTION

- 1.1 Cinotech Consultants Limited (Cinotech) was commissioned by Civil Engineering and Development Department (CEDD) as the Environmental Team (ET) to undertake environmental monitoring and auditing services for the Works Contracts involved in the implementation of Tseung Kwan O – Lam Tin Tunnel (TKO-LTT) project to ensure that the environmental performance of the Works Contracts comply with the requirements specified in the Environmental Permit (EP), Environmental Monitoring & Audit (EM&A) Manual, Environmental Impact Assessment (EIA) Report of the TKO-LTT project and other relevant statutory requirements. This is the 18th Monthly EM&A report summarizing the EM&A works for the Project in April 2018.

Purpose of the Report

- 1.2 This is the 18th Monthly EM&A Report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period in April 2018.

Structure of the Report

- 1.3 The structure of the report is as follows:

Section 1: **Introduction** – purpose and structure of the report.

Section 2: **Contract Information** – summarises background and scope of the Contract, site description, project organization and contact details, construction programme, the construction works undertaken and the status of Environmental Permits/Licenses during the reporting month.

Section 3: **Air Quality Monitoring** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, monitoring results and Event / Action Plans.

Section 4: **Noise Monitoring** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, monitoring results and Event / Action Plans.

Section 5: **Water Quality Monitoring** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, monitoring results and Event / Action Plans.

Section 6: **Ecological Monitoring** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations and Action and Limit Levels, monitoring results and Event / Action Plans.

Section 7: **Cultural Heritage** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations and monitoring results.

Section 8: **Landscape and Visual Monitoring Requirements** – summarises the

requirements of landscape and visual monitoring

Section 9: **Landfill Gas Monitoring** – summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, monitoring results and Limit Levels and Action Plan

Section 10: **Environmental Site Inspection** – summarises the audit findings of the weekly site inspections undertaken within the reporting month.

Section 11: **Waste Management** – summarises the waste management data in the reporting month.

Section 12: **Environmental Non-conformance** – summarises any monitoring exceedance, environmental complaints, environmental summons and successful prosecutions within the reporting month.

Section 13: **Future Key Issues** – summarises the impact forecast and monitoring schedule for the next three months.

Section 14: **Conclusions and Recommendation**

2. PROJECT INFORMATION**Background**

- 2.1 In 2002, Civil Engineering and Development Department (CEDD) commissioned an integrated planning and engineering study under Agreement No. CE 87/2001 (CE) “Further Development of Tseung Kwan O – Feasibility Study” (the “TKO Study”) to formulate a comprehensive plan for further development of TKO New Town. It recommended to further develop TKO to house a total population of 450,000 besides the district’s continuous commercial and industrial developments.
- 2.2 At present, the Tseung Kwan O Tunnel is the main connection between Tseung Kwan O (TKO) and other areas in the territory. To cope with the anticipated transport need, the TKO Study recommended the provision of Tseung Kwan O – Lam Tin Tunnel (TKO-LTT) (hereinafter referred to as “the Project”) and Cross Bay Link (CBL) to meet the long-term traffic demand between TKO and the external areas. The site layout plan for the Project is shown in **Figure 1**.
- 2.3 The Environmental Impact Assessment (EIA) Report for the TKO-LTT project was approved under the Environmental Impact Assessment Ordinance (EIAO) in July 2013. The corresponding Environmental Permit (EP) was issued in August 2013 (EP no.: EP-458/2013). Variations to the EP was applied and the latest EP (EP no.: EP-458/2013/C) was issued by the Director of Environmental Protection (DEP) in January 2017.
- 2.4 The commencement dates of construction of this Project is:
- Contract No. NE/2015/01 and Contract No. NE/2015/02: 7 November 2016.
 - Contract No. NE/2015/03: 29 May 2017.
 - Contract No. NE/2017/02: 15 March 2018.
 - Contract No. NE/2017/01: 23 April 2018.

Project Organizations

- 2.5 Different parties with different levels of involvement in the project organization include:
- Project Proponent – Civil Engineering and Development Department (CEDD)
 - The Engineer and the Engineer’s Representative (ER) – AECOM
 - Environmental Team (ET) – Cinotech Consultants Limited (Cinotech)
 - Independent Environmental Checker (IEC) – AnewR Consulting Limited (AnewR)
- 2.6 The key contacts of the Project are shown in **Table 2.1**.

Table 2.1 Key Project Contacts

Party	Role	Contact Person	Phone No.	Fax No.
CEDD	Project Proponent	Mr. Chiang Nin Tat, Eric	2301 1384	2739 0076
AECOM	Engineer’s Representative	Mr. KY Chan	3922 9000	2759 1698
Cinotech	Environmental Team	Dr. Priscilla Choy	2151 2089	3107 1388
		Ms. Ivy Tam	2151 2090	

AnewR	Independent Environmental Checker	Mr. Adi Lee	2618 2836	3007 8648
-------	-----------------------------------	-------------	-----------	-----------

Construction Activities undertaken during the Reporting Month

2.7 The major site activities undertaken in the reporting month included:

Table 2.2 Summary Table for Major Site Activities in the Reporting Month

Contract No.	Project Title	Site Activities (April 2018)	
NE/2015/01	Tseung Kwan O – Lam Tin Tunnel – Main Tunnel and Associated Works	Lam Tin Interchange	1. EHC2 U-Trough 2. Site Formation – Area 1G1, Area 1G2, Area 2, Area 3, Area 4 & Area 5 3. Pipe Pile wall – Area 2A
		Main Tunnel	1. Main tunnel Excavation
		TKO Interchange	1. Haul Road Construction, Site Formation and Slope Works 2. Steel Platform for Bridge Construction
NE/2015/02	Tseung Kwan O – Lam Tin Tunnel – Road P2 and Associated Works	1) Installation of DN2100 Concrete Pipe at Portion IV & VII 2) ELS Installation for U-Trough at Portion V & VI 3) Construction of Retaining Wall and U-Trough at Portion VIII 4) Enhancement of Temporary Steel Cofferdam at Portion IX 5) Dredging Works and Armour Rock Removal at Portion IX 6) Treatment of Marine Sediment at Area A 7) General Site Clearance and Hoarding Erection	
NE/2015/03	Tseung Kwan O – Lam Tin Tunnel – Northern Footbridge	1. Erection of falsework system	
NE/2017/01	Tseung Kwan O – Lam Tin Tunnel – Tseung Kwan O Interchange and Associated Works	1. Construction of Site Office	
NE/2017/02	Tseung Kwan O – Lam Tin Tunnel – Road P2/D4 and Associated Works	1) Trial pit 2) Underground utilities detection 3) Temporary traffic arrangement Setup 4) Site office erection 5) Communication Liaison Center erection 6) Modification of traffic island 7) Fencing erection	

2.8 The construction programme showing the inter-relationship with environmental protection/mitigation measures are presented in **Table 2.3**.

Table 2.3 Construction Programme Showing the Inter-Relationship with Environmental Protection/Mitigation Measures

Construction Works	Major Environmental Impact	Control Measures
As mentioned in Table 2.2	Noise, dust impact, water quality and waste generation	<ul style="list-style-type: none"> Sufficient watering of the works site with active dust emitting activities Properly cover the stockpiles On-site waste sorting and implementation of trip ticket system Appropriate desilting/sedimentation devices provided on site for treatment before discharge Use of quiet plant and well-maintained construction plant Provide movable noise barrier

Status of Environmental Licences, Notification and Permits

2.9 A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project is presented in Table 2.4.

Table 2.4 Summary of the Status of Environmental Licences, Notification and Permits

Contract No.	Permit / License No.	Valid Period		Status
		From	To	
Environmental Permit (EP)				
N/A	EP-458/2013/C	20/1/2017	N/A	Valid
Notification pursuant to Air Pollution Control (Construction Dust) Regulation				
NE/2015/01	EPD Ref no.: 405305	21/07/2016	N/A	Valid
	EPD Ref no.: 405582	28/07/2016	N/A	Valid
NE/2015/02	EPD Ref no.: 406100	12/08/2016	N/A	Valid
NE/2015/03	EPD Ref no.: 416072	26/04/2017	N/A	Valid
NE/2017/02	EPD Ref no.: 429867	19/01/2018	N/A	Valid
NE/2017/01	EPD Ref no.: 430070	25/01/2018	N/A	Valid
Billing Account for Construction Waste Disposal				
NE/2015/01	Account No. 7025431	11/07/2016	N/A	Valid
NE/2015/02	Account No. 7025654	16/08/2016	N/A	Valid
NE/2015/03	Account No. 7026805	30/12/2016	N/A	Valid
NE/2017/02	Account No. 7029651	22/12/2017	N/A	Valid
NE/2017/01	Account No. 7029994	01/02/2018	N/A	Valid
Vessel Billing Account under construction waste disposal charging scheme				
NE/2015/01	Account No. 7027764	29/01/2018	10/05/2018	Valid
Registration of Chemical Waste Producer				
NE/2015/01	Waste Producer No. 5218-290-L2881-02	22/08/2016	N/A	Valid
	Waste Producer No. 5213-833-L2532-03	22/08/2016	N/A	Valid
NE/2015/02	Waste Producer No. 5213-838-C4094-01	23/08/2016	N/A	Valid

Contract No.	Permit / License No.	Valid Period		Status
		From	To	
NE/2015/03	Waste Producer No. 5213-265-W3435-04	19/07/2017	N/A	Valid
NE/2017/02	Waste Producer No. 5213-833-Z4004-04	01/02/2018	N/A	Valid
NE/2017/01	Waste Producer No. 5213-833-C4262-01	12/02/2018	N/A	Valid
Effluent Discharge License under Water Pollution Control Ordinance				
NE/2015/01	WT00025806-2016	22/11/2016	30/11/2021	Valid
	WT00026212-2016	09/11/2017	30/11/2021	Valid
	WT00027354-2017	22/03/2017	31/03/2022	Valid
	WT00027405-2017	22/03/2017	31/03/2022	Valid
	WT-00028495-2017	11/08/2017	31/08/2022	Valid
NE/2015/02	WT00026386-2016	15/12/2016	31/12/2021	Valid
	WT00027226-2017	23/02/2017	28/02/2022	Valid
NE/2015/03	WT00027295-2017	20/03/2017	18/04/2019	Valid
	WT00027266-2017	08/03/2017	18/04/2019	Valid
NE/2017/01	WT00030711-2018	11/04/2018	30/04/2023	Valid
NE/2017/02	WT00030654-2018	16/04/2018	30/04/2023	Valid
Construction Noise Permit (CNP)				
NE/2015/01	GW-RE1024-17	23/12/2017	22/06/2018	Valid
	GW-RE0084-18	10/02/2018	07/05/2018	Valid
	GW-RE0125-18	25/02/2018	24/05/2018	Valid
	GW-RE0142-18	08/03/2018	04/05/2018	Valid
	GW-RE0141-18	02/03/2018	31/05/2018	Valid
	GW-RE0140-18	06/03/2018	05/09/2018	Valid
	GW-RE0278-18	26/04/2018	24/06/2018	Valid
NE/2015/02	GW-RE0800-17	11/10/2017	10/04/2018	Expired on 10/04/2018
	GW-RE0809-17	13/10/2017	12/04/2018	Expired on 12/04/2018
	GW-RE0905-17	17/11/2017	15/05/2018	Valid
	GW-RE0038-18	30/01/2018	29/04/2018	Expired on 29/04/2018
	GW-RE0869-17	04/11/2017	30/04/2018	Expired on 30/04/2018
	GW-RE0916-17	02/12/2017	01/06/2018	Valid
NE/2015/03	GW-RE0966-17	14/03/2018	14/04/2018	Expired on 14/04/2018
	GW-RE0162-18	27/03/2018	27/04/2018	Expired on 27/04/2018
	GW-RE0254-18	28/04/2018	20/05/2018	Valid

Contract No.	Permit / License No.	Valid Period		Status
		From	To	
Marine Dumping Permit				
NE/2015/02	EP/MD/18-129	16/03/2018	15/09/2018	Valid
	EP/MD/18-134	01/04/2018	30/04/2018	Valid
Specified Process (SP) License				
NE/2015/01	L-11-053	09/03/2018	08/03/2021	Valid

Summary of EM&A Requirements

- 2.10 The EM&A programme requires construction noise monitoring, air quality monitoring, water quality monitoring, environmental site audit, etc. The EM&A requirements for each parameter are described in the following sections, including:
- All monitoring parameters;
 - Action and Limit levels for all environmental parameters;
 - Event Action Plans;
 - Environmental mitigation measures, as recommended in the Project EIA Report.
- 2.11 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 10 of this report.
- 2.12 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the monitoring parameters of the required environmental monitoring works and audit works for the Project in April 2018.

3. AIR QUALITY

Monitoring Requirements

- 3.1 According to EM&A Manual of the Project, 1-hour and 24-hour TSP monitoring are required to monitor the air quality. For regular impact monitoring, a sampling frequency of at least once in every six days shall be undertaken at all of the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six days shall be undertaken when the highest dust impact occurs. **Appendix A** shows the established Action/Limit Levels for the environmental monitoring works.

Monitoring Locations

- 3.2 Six designated monitoring stations were selected for air quality monitoring programme. **Table 3.1** describes the air quality monitoring locations, which are also depicted in **Figure 2**.

Table 3.1 Locations for Air Quality Monitoring

Monitoring Stations	Location	Location of Measurement
AM1	Tin Hau Temple	Ground Level
AM2	Sai Tso Wan Recreation Ground	Ground Level
AM3	Yau Lai Estate Bik Lai House	Rooftop (41/F)
AM4 ⁽¹⁾	Sitting-out Area at Cha Kwo Ling Village	Ground Level
AM4(A) ^{(2) (*)}	Cha Kwo Ling Public Cargo Working Area Administrative Office	Rooftop (3/F)
AM5(A) ^(*)	Tseung Kwan O DSD Desilting Compound	Ground Level
AM6(A) ^(*)	Park Central, L1/F Open Space Area	1/F

Remarks: (1) For 1-hour TSP monitoring; (2) For 24-hour TSP monitoring

(*) Air quality monitoring at designated station AM4(24-hr TSP), AM5 and AM6 was rejected by the premise owners. Therefore, baseline and impact air quality monitoring works were carried out at alternative air quality monitoring stations AM4(A) (24-hr TSP only), AM5(A) and AM6(A) respectively.

Monitoring Equipment

- 3.3 High Volume Samplers (HVS) were used to carry out 24-hour TSP monitoring. Direct reading dust meter were also used to measure 1-hour average TSP levels. The 1-hour sampling was determined periodically by HVS to check the validity and accuracy of the results measured by direct reading method.
- 3.4 Wind data monitoring equipment was set at rooftop (about 41/F) of Yau Lai Estate Bik Lai House for logging wind speed and wind direction such that the wind sensors are clear of obstructions or turbulence caused by building. The wind data monitoring equipment is re-calibrated at least once every six months and the wind directions are divided into 16 sectors of 22.5 degrees each. The location is shown in **Figure 2**.
- 3.5 **Table 3.2** summarizes the equipment to be used in the air quality monitoring. Copies of calibration certificates are attached in **Appendix B**.

Table 3.2 Air Quality Monitoring Equipment

Equipment	Model and Make	Quantity
Calibrator	TISCH Model: TE-5025A	1
1-hour TSP Dust Meter	Sibata Model No.: LD-3 / LD-3B	0
	Met One Instruments Model No.: AEROCET-531	0
	Handheld Particle Counter Hal-HPC300 / Hal-HPC301	6
HVS Sampler	TISCH Model: TE-5170	1
	GMW Model: GS2310	5
Wind Anemometer	Davis Weather Monitor II, Model no. 7440	0
	Davis Weather Stations, Vantage Pro 2, Model No. 6152CUK	1

Monitoring Parameters and Frequency

- 3.6 **Table 3.3** summarizes the monitoring parameters, monitoring period and frequencies of air quality monitoring.

Table 3.3 Frequency and Parameters of Air Quality Monitoring

Monitoring Stations	Parameter	Frequency
AM1, AM2, AM3, AM4, AM5(A) and AM6(A)	1-hour TSP	3 times per 6 day
AM1, AM2, AM3, AM4(A), AM5(A) and AM6(A)	24-hour TSP	Once per 6 days

Monitoring Methodology***1-hour TSP Monitoring****Measuring Procedures*

- 3.7 The measuring procedures of the 1-hour dust meter are in accordance with the Manufacturer's Instruction Manual as follows:

(Model LD3 / LD3B)

- The 1-hour dust meter is placed at least 1.3 meters above ground.
- Set POWER to "ON" and make sure that the battery level was not flash or in low level.
- Allow the instrument to stand for about 3 minutes and then the cap of the air sampling inlet has been released.
- Push the knob at MEASURE position.
- Set time/mode setting to [BG] by pushing the time setting switch. Then, start the background measurement by pushing the start/stop switch once. It will take 6 sec. to complete the background measurement.
- Push the time setting switch to change the time setting display to [MANUAL] at the bottom left of the liquid crystal display. Finally, push the start/stop switch to stop the measuring after 1 hour sampling.
- Information such as sampling date, time, count value and site condition were recorded during the monitoring period.

(AEROCET-531)

- The 1-hour dust meter is placed at least 1.3 meters above ground.
- Remove the red rubber cap from the AEROCET-531 inlet nozzle.

- Turn on the power switch that is located on the right side of the AEROCET-531.
- On power up the product intro screen is displayed for 3 seconds. The intro screen displays the product name and firmware version.
- Then the main counter screen will be displayed.
- Press the START button. Internal vacuum pump start running. After 1 minute the pump will stop and the 0.5 μ m and 5 μ m channels will show the cumulative counts of particles larger than 0.5 μ m and 5 μ m per cubic foot.
- The AEROCET-531 is now checked out and ready for use.
- To switch off the AEROCET-531 power to stop the measuring after 1 hour sampling.
- Information such as sampling date, time, and display value and site condition were recorded during the monitoring period.

(Equipment: Hal Technology; Model no. Hal-HPC300 / Hal-HPC301)

- The 1-hour dust meter is placed at least 1.3 meters above ground.
- Set POWER to “ON” and make sure that the battery level was not flash or in low level.
- Allow the instrument to stand for about 3 minutes and then the cap of the air sampling inlet has been released.
- Push the knob at MEASURE position.
- Set time/mode setting to [BG] by pushing the time setting switch. Then, start the background measurement by pushing the start/stop switch once. It will take 6 sec. to complete the background measurement.
- Push the time setting switch to change the time setting display to [MANUAL] at the bottom left of the liquid crystal display. Finally, push the start/stop switch to stop the measuring after 1 hour sampling.
- Information such as sampling date, time, count value and site condition were recorded during the monitoring period.

Maintenance/Calibration

3.8 The following maintenance/calibration is required for the direct dust meters:

- Check and calibrate the meter by HVS to check the validity and accuracy of the results measured by direct reading method at 2-month intervals throughout all stages of the air quality monitoring.

24-hour TSP Monitoring

Instrumentation

3.9 High volume samplers (HVS) (TISCH Model: TE-5170 and GMW Model: GS2310) completed with appropriate sampling inlets were employed for 24-hour TSP monitoring. The sampler is composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complied with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

3.10 The positioning of the HVS samplers are as follows:

- a horizontal platform with appropriate support to secure the samplers against gusty wind shall be provided;
- no two samplers shall be placed less than 2 meter apart
- the distance between the sampler and an obstacle, such as buildings, must be at least twice the height that the obstacle protrudes above the sampler;
- a minimum of 2 metres of separation from walls, parapets and penthouses is required for rooftop samplers;

- a minimum of 2 metres of separation from any supporting structure, measured horizontally is required;
- no furnace or incinerator flue is nearby;
- airflow around the sampler is unrestricted;
- the sampler is more than 20 metres from the dripline;
- any wire fence and gate, to protect the sampler, shall not cause any obstruction during monitoring;
- permission must be obtained to set up the samplers and to obtain access to the monitoring stations; and
- a secured supply of electricity is needed to operate the samplers.

Operating/analytical procedures for the operation of HVS

- 3.11 Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 1.1 m³/min. and 1.4 m³/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50.
- 3.12 For TSP sampling, fiberglass filters with a collection efficiency of > 99% for particles of 0.3µm diameter were used.
- 3.13 The power supply was checked to ensure the sampler worked properly. On sampling, the sampler was operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air monitoring station.
- 3.14 The filter holding frame was then removed by loosening the four nuts and a weighted and conditioned filter was carefully centered with the stamped number upwards, on a supporting screen.
- 3.15 The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- 3.16 The shelter lid was closed and secured with the aluminum strip.
- 3.17 The timer was then programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).
- 3.18 After sampling, the filter was removed and sent to the HOKLAS laboratory (Wellab Ltd.) for weighing. The elapsed time will be also recorded.
- 3.19 Before weighing, all filters was equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than ±3°C; the relative humidity (RH) should be < 50% and not vary by more than ±5%. A convenient working RH is 40%.

Maintenance/Calibration

- 3.20 The following maintenance/calibration is required for the HVS:
- The high volume motors and their accessories will be properly maintained. Appropriate maintenance such as routine motor brushes replacement and electrical wiring checking will be made to ensure that the equipment and necessary power supply are in good working condition.

- High volume samplers will be calibrated at bi-monthly intervals using TE-5025A Calibration Kit throughout all stages of the air quality monitoring.

Results and Observations

- 3.21 All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 3.22 All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 3.23 The air temperature, precipitation and the relative humidity data was obtained from Hong Kong Observatory where the wind speed and wind direction were recorded by the installed Wind Anemometer at rooftop of Yau Lai Estate Bik Lai House (41/F). The location is shown in **Figure 2**. This weather information for the reporting month is summarized in **Appendix C**.
- 3.24 The monitoring data and graphical presentations of 1-hour and 24-hour TSP monitoring results are shown in **Appendix E** and **Appendix F** respectively.
- 3.25 The summary of exceedance record in reporting month is shown in **Appendix K**. No exceedance was recorded for the air quality monitoring.
- 3.26 According to our field observations, the major dust source identified at the designated air quality monitoring stations are as follows:

Table 3.4 Major Dust Source during Air Quality Monitoring

Station	Major Dust Source
AM1 – Tin Hau Temple	Road Traffic at Cha Kwo Ling Road
AM2 – Sai Tso Wan Recreation Ground	N/A
AM3 – Yau Lai Estate Bik Lai House	Road Traffic near Eastern Cross Harbour Tunnel Toll Plaza
AM4 - Sitting-out Area at Cha Kwo Ling Village	Road Traffic at Cha Kwo Ling Road
AM4(A) - Cha Kwo Ling Public Cargo Working Area Administrative Office	Road Traffic at Cha Kwo Ling Road
AM5(A) - Tseung Kwan O DSD Desilting Compound	Vehicle Movement within the Desilting Compound
AM6(A) - Park Central, L1/F Open Space Area	Road Traffic at Po Yap Road

4. NOISE**Monitoring Requirements**

- 4.1 According to EM&A Manual of the Project, construction noise monitoring was conducted to monitor the construction noise arising from the construction activities. The regular monitoring frequency for each monitoring station shall be on a weekly basis and conduct one set of measurements between 0700 and 1900 hours on normal weekdays. **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.

Monitoring Locations

- 4.2 Noise monitoring was conducted at 8 designated monitoring stations (CM1, CM2, CM3, CM4, CM5, CM6(A), CM7(A), CM8(A)) in the reporting period. **Table 4.1** and **Figure 3** show the locations of these stations.

Table 4.1 Noise Monitoring Stations

Monitoring Stations	Locations	Location of Measurement
CM1	Nga Lai House, Yau Lai Estate Phase 1, Yau Tong	Rooftop (41/F)
CM2	Bik Lai House, Yau Lai Estate Phase 1, Yau Tong	Rooftop (41/F)
CM3	Block S, Yau Lai Estate Phase 5, Yau Tong	Rooftop (40/F)
CM4	Tin Hau Temple, Cha Kwo Ling	Ground Level
CM5	CCC Kei Faat Primary School, Yau Tong	Rooftop (6/F)
CM6(A)*	Site Boundary of Contract No. NE/2015/02 near Tower 1, Ocean Shores	Ground Level
CM7(A)*	Site Boundary of Contract No. NE/2015/02 near Tower 7, Ocean Shores	Ground Level
CM8(A)*	Park Central, L1/F Open Space Area	1/F

Remarks: * Noise monitoring at designated station CM6, CM7 & CM8 was rejected by the premise owners. Therefore, baseline and impact noise monitoring works were carried out at alternative noise monitoring stations CM6(A), CM7(A) and CM8(A) respectively.

Monitoring Equipments

- 4.3 Integrating Sound Level Meter was used for impact noise monitoring. The meters are Type 1 sound level meter capable of giving a continuous readout of the noise level readings including equivalent continuous sound pressure level (L_{eq}) and percentile sound pressure level (L_x) that also complied with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications. **Table 4.2** summarizes the noise monitoring equipment being used. Copies of calibration certificates are attached in **Appendix B**.

Table 4.2 Noise Monitoring Equipment

Equipment	Model and Make	Quantity
Integrating Sound Level Meter	SVAN 955 / 957 / 977	4
	BSWA 801	1
Calibrator	SV30A	2
	Brüel & Kjær 4231	2

- 4.4 **Table 4.3** summarizes the monitoring parameters, frequency and total duration of monitoring. The noise monitoring schedule is shown in **Appendix D**.

Table 4.3 Frequency and Parameters of Noise Monitoring

Monitoring Stations	Parameter	Period	Frequency	Measurement
CM1	L ₁₀ (30 min) dB(A) L ₉₀ (30 min) dB(A) L _{eq} (30 min) dB(A)	0700-1900 hrs on normal weekdays	Once per week	Façade
CM2				Façade
CM3				Façade
CM4				Façade
CM5				Façade
CM6(A)				Free Field
CM7(A)				Free Field
CM8(A)				Façade

Monitoring Methodology and QA/QC Procedure

- 4.5 The monitoring procedures are as follows:
- The monitoring station was normally be at a point 1m from the exterior of the sensitive receivers building façade and be at a position 1.2m above the ground.
 - For free field measurement, the meter was positioned away from any nearby reflective surfaces. All records for free field noise levels was adjusted with a correction of +3 dB(A).
 - The battery condition was checked to ensure the correct functioning of the meter.
 - Parameters such as frequency weighting, the time weighting and the measurement time was set as follows:
 - frequency weighting : A
 - time weighting : Fast
 - measurement time : 30 minutes
 - Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement will be more than 1.0 dB, the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.
 - At the end of the monitoring period, the L_{eq}, L₉₀ and L₁₀ was recorded. In addition, noise sources was recorded on a standard record sheet.
 - Noise monitoring will be cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s. Supplementary monitoring was provided to ensure sufficient data would be obtained.

Maintenance and Calibration

- 4.6 The microphone head of the sound level meter and calibrator was cleaned with a soft cloth at quarterly intervals.
- 4.7 The sound level meter and calibrator was checked and calibrated at yearly intervals.
- 4.8 Immediately prior to and following each noise measurement the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration levels from before and after the noise measurement agree to within 1.0 dB.

Results and Observations

- 4.9 All noise monitoring was conducted as scheduled in the reporting month. Thirteen (13) Action Level exceedance was recorded due to the documented complaints received in this reporting month. No Limit Level exceedance was recorded in the reporting month.
- 4.10 Noise monitoring results and graphical presentations are shown in **Appendix G**.
- 4.11 The major noise source identified at the noise monitoring stations are shown in **Table 4.4**.

Table 4.4 Major Noise Source during Noise Monitoring

Monitoring Stations	Locations	Major Noise Source
CM1	Nga Lai House, Yau Lai Estate Phase 1, Yau Tong	Road Traffic near Eastern Cross Harbour Tunnel Toll Plaza
CM2	Bik Lai House, Yau Lai Estate Phase 1, Yau Tong	Road Traffic near Eastern Cross Harbour Tunnel Toll Plaza
CM3	Block S, Yau Lai Estate Phase 5, Yau Tong	Road Traffic near Eastern Cross Harbour Tunnel Toll Plaza
CM4	Tin Hau Temple, Cha Kwo Ling	Road Traffic at Cha Kwo Ling Road
CM5	CCC Kei Faat Primary School, Yau Tong	Road Traffic at Yau Tong Road
CM6(A)	Site Boundary of Contract No. NE/2015/02 near Tower 1, Ocean Shores	Road Traffic at O King Road near Ocean Shores
CM7(A)	Site Boundary of Contract No. NE/2015/02 near Tower 7, Ocean Shores	Road Traffic at Tong Yin Street
CM8(A)	Park Central, L1/F Open Space Area	Road Traffic at Po Yap Road

- 4.12 All the Construction Noise Levels (CNLs) reported in this report were adjusted with the corresponding baseline level (i.e. Measured L_{eq} – Baseline L_{eq} = CNL), in order to facilitate the interpretation of the noise exceedance. The baseline noise level and the Noise Limit Level at each designated noise monitoring station are presented in **Table 4.5**.

Table 4.5 Baseline Noise Level and Noise Limit Level for Monitoring Stations

Station	Baseline Noise Level, dB (A) (at 0700 – 1900 hrs on normal weekdays)	Noise Limit Level, dB (A) (at 0700 – 1900 hrs on normal weekdays)
CM1	65.5	75
CM2	63.6	
CM3	65.6	
CM4	62.0	
CM5	68.2	70*
CM6(A)	61.9	75
CM7(A)	58.3	
CM8(A)	69.1	

(*) Noise Limit Level is 65 dB(A) during school examination periods.

Updated Construction Noise Assessment

Contract No. NE/2015/01, Contract No. NE/2015/02, Contract No. NE/2015/03, Contract No. NE/2017/01 and Contract No. NE/2017/02

- 4.13 No update of Construction Noise Assessment in the reporting period. Any updated Construction Noise Assessment will be shown in **Appendix S**.

5. WATER QUALITY

Monitoring Requirements

Groundwater Quality

- 5.1 Groundwater quality monitoring shall be conducted as identified in the EIA report (locations refer to **Figure 4**, Stream 1 to 3). According to the EM&A Manual, dissolved oxygen (DO), pH, temperature, turbidity, suspended solids (SS), 5-day biochemical oxygen demand (BOD₅), Total organic carbon (TOC), Total Nitrogen, Ammonia-N and Total Phosphate are the parameters for the monitoring. **Appendix A** shows the established Action and Limit Levels.
- 5.2 As stated in the Baseline Environmental Monitoring Plan submitted to EPD in September 2016, Groundwater quality monitoring could not be conducted at the other identified monitoring station in the EIA Report, Stream 4, as it was found to be not accessible due to safety reason. EPD has no further comment on the Plan in October 2016.

Marine Water Quality

- 5.3 Marine water quality monitoring was conducted three times per week at the designated monitoring stations. Monitoring took place two times per monitoring day during mid ebb and mid flood tides at three depths (1 meter from surface, mid depth and 1 meter from the bottom). For Tseung Kwan O Salt Water Intake (i.e. Station M6), water sampling and in-situ measurements was taken at the vertical level where the water abstraction point of the intake is located (i.e. approximately mid-depth level). If the water depth is less than 6m, the mid-depth measurement may be omitted. If the depth is less than 3m, only the mid-depth measurements need to be taken.
- 5.4 Duplicate in-situ measurements (Dissolved oxygen (DO) concentration, DO saturation, turbidity, pH, temperature and salinity) and water samples (suspended solids (SS)) at each depth were monitored in accordance with the requirements in the EM&A Manual. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides were not less than 0.5m.
- 5.5 According to the Environmental Review Report (ERR) for Variations of Environmental Permit (Ref: C45-03), water quality monitoring and audit programme was implemented for monitoring of oxygen depletion (e.g. Dissolved Oxygen (DO) level) in this embayed waters during the period when the fully enclosed barrier is installed. A “Proposal for Water Quality Monitoring in Temporary Marine Embayment” has been submitted to EPD in July 2017 to propose the monitoring frequency, parameter, location, etc. EPD has no further comment on the Proposal.

Groundwater Level Monitoring (Piezometer Monitoring)

- 5.6 Daily piezometer monitoring at any time of the day shall be carried throughout the whole period when any tunnel construction activities are carried out within +/- 50m of the piezometer gate in plan. The monitoring has not commenced in this reporting period.

Monitoring Locations

Groundwater Quality

- 5.7 Stream 1 – Stream 3 is designated for the groundwater quality monitoring according to EM&A Manual. The locations are summarized in **Table 5.1** and shown on **Figure 4**.

Table 5.1 Groundwater Quality Monitoring Stations

Monitoring Streams	Descriptions	Sampling Location
Stream 1	Stream running between the Kwong Tin Estate and Lei Yue Mun Road	1 sampling location for each stream
Stream 2	Stream on western coast of Chiu Keng Wan	
Stream 3	Stream on western coast of Chiu Keng Wan	

Marine Water Quality

- 5.8 A total of twelve monitoring stations are designated for the water quality monitoring program according to EM&A Manual. One additional monitoring station (W1) is designated for monitoring of oxygen depletion in the embayed waters during the period when the fully enclosed barrier is installed. The locations are also summarized in **Table 5.2** and shown on **Figure 5** and **Figure 9**.

Table 5.2 Marine Water Quality Monitoring Stations

Monitoring Stations	Descriptions	Coordinates	
		Easting	Northing
M1	Junk Bay Coral Site – Junk Bay near Chiu Keng Wan	844255	817565
M2	Junk Bay Coral Site – Junk Bay	844076	817087
M3	Junk Bay Coral Site – Junk Island	844491	817890
M4	Junk Bay Coral Site – Chiu Keng Wan	843209	816416
M5	Junk Bay Coral Site – Fat Tong Chau	845463	815769
M6	Tseung Kwan O Salt Water Intake	845512	817442
C1	Control Station – Southeast	844696	814773
C2	Control Station – Northwest	842873	816014
G1	Gradient Station	844418	817560
G2	Gradient Station	844290	817384
G3	Gradient Station	844488	817735
G4	Gradient Station	844967	817551
W1	Ocean Shores (for WQM in temporary marine embayment)	844324	817791

Monitoring Equipments

- 5.9 For in-situ monitoring, a multi-parameter meter (Aquaread AP-2000-D) was used to measure Dissolved oxygen (DO) concentration, DO saturation (DO %), pH, temperature and turbidity. A sampler was used to collect water samples for laboratory analysis of SS, BOD₅, TOC, Total Nitrogen, Ammonia-N and Total Phosphate.

Dissolved Oxygen (DO) and Temperature Measuring Equipment

- 5.10 The instrument for measuring dissolved oxygen and temperature was portable and weatherproof complete with cable, sensor, comprehensive operation manuals and use DC power source. It was capable of measuring:
- a dissolved oxygen level in the range of 0-20 mg/L and 0-200% saturation; and

- a temperature of 0-45 degree Celsius.
- 5.11 It has a membrane electrode with automatic temperature compensation complete with a cable.
- 5.12 Sufficient stocks of spare electrodes and cables were available for replacement where necessary.
- 5.13 Salinity compensation was built-in in the DO equipment.

Turbidity

- 5.14 Turbidity was measured in-situ by the nephelometric method. The instrument was portable and weatherproof using a DC power source complete with cable, sensor and comprehensive operation manuals. The equipment was capable of measuring turbidity between 0-1000 NTU. The probe cable was not be less than 25m in length.

pH

- 5.15 The instrument was consisting of a potentiometer, a glass electrode, a reference electrode and a temperature-compensating device. It was readable to 0.1pH in a range of 0 to 14. Standard buffer solutions of at least pH 7 and pH 10 were used for calibration of the instrument before and after use.

Water Depth Detector

- 5.16 A portable, battery-operated echo sounder was used for the determination of water depth at each designated monitoring station.

Water Sampler

- 5.17 Water samples collected for laboratory analysis were stored in high density polythene bottles sample containers, with appropriate preservatives added. All sampling bottles were labeled (waterproof) with the sampling date and time, sample lot number and sampling location reference number to avoid mishandling.

Sample Container and Storage

- 5.18 Following collection, water samples for laboratory analysis were stored in high density polythene bottles, with preservative appropriately added where necessary. They will be packed in ice (cooled to 4°C without being frozen), delivered to the laboratory and analysed as soon as possible.

Calibration of In-Situ Instruments

- 5.19 All in-situ monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or other international accreditation scheme before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the water quality monitoring.
- 5.20 For the on-site calibration of field equipment, the BS 1427:1993, "Guide to Field and on-site test methods for the analysis of waters" was observed.
- 5.21 Before each round of monitoring, a zero check in distilled water was performed with the turbidity probe of Aquaread AP-2000-D. The probe was then be calibrated with a solution of known NTU.
- 5.22 Sufficient stocks of spare parts were maintained for replacements when necessary. Backup monitoring equipment was also made available so that monitoring can proceed

- uninterrupted even when some equipment is under maintenance, calibration, etc.
- 5.23 **Table 5.3** summarizes the equipment used in the water quality monitoring program. Copies of the calibration certificates of the equipment are shown in **Appendix B**.

Table 5.3 Water Quality Monitoring Equipment

Equipment	Model and Make	Qty.
Water Sampler	Kahlsico Water-Bottle Model 135DW 150	1
Multi-parameter Water Quality System	YSI 6820-C-M	0
	Aquaread AP-2000-D	0
	YSI EXO1 Multiparameter Sondes	4
Monitoring Position Equipment	“Magellan” Handheld GPS Model GPS-320	1
Water Depth Detector	Fishfinder 140	1

Monitoring Parameters and Frequency

- 5.24 **Table 5.4** summarizes the monitoring parameters, monitoring period and frequencies of the water quality monitoring in the reporting period.

Table 5.4 Water Quality Monitoring Parameters and Frequency

Monitoring Stations	Parameters, unit	Depth	Frequency
Groundwater Quality			
Stream 1- Stream 3	<ul style="list-style-type: none"> • DO, mg/L • DO Saturation, % • pH • Water Temperature (°C) • Turbidity, NTU • SS, mg/L • BOD₅, mg O₂/L • TOC, mg-TOC/L • Total Nitrogen, mg/L • Ammonia-N, mg NH₃-N/L • Total Phosphate, mg-P/L 	Mid-depth	Biweekly (When the tunnel construction works are found within 50m of the location, weekly.)
Marine Water Quality			
M1 M2 M3 M4 M5 M6 C1 C2 G1 G2 G3 G4	<p><i>In-situ:</i> Dissolved oxygen (DO) concentration, DO saturation, turbidity, pH, temperature and salinity</p> <p><u>Laboratory Testing:</u> Suspended Solids (SS)</p>	<p><u>M1-M5, C1-C2, G1-G4</u></p> <ul style="list-style-type: none"> • 3 water depths: 1m below water surface, mid-depth and 1m above sea bed. • If the water depth is less than 3m, mid-depth sampling only. • If the water depth is less than 6m, omit mid-depth sampling. <p><u>M6</u></p> <ul style="list-style-type: none"> • at the vertical level where the water abstraction point of the intake is located(i.e. approximately mid-depth level) 	3 days per week / 2 per monitoring day (1 for mid-ebb and 1 for mid-flood)

Monitoring Stations	Parameters, unit	Depth	Frequency
Water Quality Monitoring in Temporary Marine Embayment			
W1	<ul style="list-style-type: none"> • DO, mg/L • DO Saturation, % • pH • Water Temperature (°C) • Salinity, ppt 	<ul style="list-style-type: none"> • 3 water depths: 1m below water surface, mid-depth and 1m above sea bed. • If the water depth is less than 3m, mid-depth monitoring only. • If the water depth is less than 6m, omit mid-depth monitoring 	Weekly during the period when the fully enclosed barrier is installed

Monitoring Methodology

Groundwater Quality

- 5.25 At each monitoring location, two consecutive in-situ measurements for DO concentration, DO saturation, pH, temperature and turbidity were taken for water samples on site. The probes were retrieved out of the water after the first measurement and then re-deployed for the second measurement. Where the difference in the value between the first and second readings of each set was more than 25% of the value of the first reading, the reading was discarded and further readings were taken.
- 5.26 For SS, BOD₅, TOC, Total Nitrogen, Ammonia-N and Total Phosphate, measurement and grab samples of surface water was collected. Water samples of about adequate volume was collected and stored in high density polythene bottles. Following collection, water samples was stored in high density polythene bottles. Preservation H₂SO₄ was appropriately added for water samples for TOC, Total Nitrogen, Ammonia-N and Total Phosphate testing. Water samples was packed in ice and cooled to 4°C (without being frozen), delivered to the HOKLAS accredited laboratory, Wellab Limited and analyzed.

Marine Water Quality

- 5.27 The monitoring stations were accessed using survey boat by the guide of a hand-held Global Positioning System (GPS). The depth of the monitoring location was measured using depth meter in order to determine the sampling depths. Afterwards, the probes of the in-situ measurement equipment was lowered to the predetermined depths (1 m below water surface, mid-depth and 1 m above seabed) and the measurements was carried out accordingly. The in-situ measurements at predetermined depths was carried out in duplicate. In case the difference in the duplicate in-situ measurement results was larger than 25%, the third set of in-situ measurement would be carried out for result confirmation purpose.
- 5.28 Water sampler was lowered into the water to the required depths of sampling. Upon reaching the pre-determined depth, a messenger to activate the sampler was then released to travel down the wire. The water sample was sealed within the sampler before retrieving. At each station, water samples for SS at three depths (1 m below water surface, mid-depth and 1 m above seabed) were collected accordingly. Water samples were stored in a cool box and kept at less than 4°C but without frozen and sent to the laboratory as soon as possible.

Laboratory Analytical Methods

- 5.29 The testing of all parameters were conducted by Wellab Ltd. (HOKLAS Registration No.083) and comprehensive quality assurance and control procedures in place in order to ensure quality and consistency in results. The testing method and limit of reporting are provided in **Table 5.5**.

Table 5.5 Methods for Laboratory Analysis for Water Samples

Parameters (Unit)	Proposed Method	Reporting Limit	Detection Limit
SS (mg/L)	APHA 2540 D	0.5 mg/L ⁽¹⁾	0.5 mg/L
BOD ₅ (mg O ₂ /L)	APHA 19ed 5210B	2 mg O ₂ /L	--
TOC (mg-TOC/L)	In-house method SOP020 (Wet Oxidation)	1 mg-TOC/L	--
Total Nitrogen (mg/L)	In-house method SOP063 (FIA)	0.6 mg/L	--
Ammonia-N (mg NH ₃ -N/L)	In-house method SOP057 (FIA)	0.05 mg NH ₃ - N/L	--
Total Phosphorus (mg-P/L) ⁽²⁾	In-house method SOP055 (FIA)	0.05 mg-P/L	--

Note:

1) Limit of Reporting is reported as Detection Limit for non-HOKLAS report.

2) Parameter Total Phosphorus represents the laboratory testing for total phosphate content in water which is the sum of all three forms of phosphates in water.

QA/QC Requirements

Decontamination Procedures

- 5.30 Water sampling equipment used during the course of the monitoring programme was decontaminated by manual washing and rinsed clean seawater/distilled water after each sampling event. All disposal equipment was discarded after sampling.

Sampling Management and Supervision

- 5.31 Water samples were dispatched to the testing laboratory for analysis as soon as possible after the sampling. All samples were stored in a cool box and kept at less than 4°C but without frozen. All water samples were handled under chain of custody protocols and relinquished to the laboratory representatives at locations specified by the laboratory.
- 5.32 QA/QC procedures as attached in **Appendix J** are available for the parameters analyzed in the HOKLAS-accredited laboratory, WELLAB Ltd.

Results and Observations

Groundwater Quality Monitoring

- 5.33 All groundwater quality monitoring was conducted as scheduled in the reporting month. Summary of groundwater quality monitoring results is shown in **Table 5.6**. Groundwater monitoring results, graphical presentations and laboratory testing reports are shown in **Appendix H**.
- 5.34 Other relevant data was also recorded, such as monitoring location / position, time, sampling depth, weather conditions and any special phenomena or work underway nearby.

- 5.35 Action and Limit Level for groundwater monitoring has been reviewed with consideration of monitoring results obtained from November 2016 to June 2017, as there was no tunnel boring or tunnel construction works from November 2016 to June 2017. A “Review Report for Action and Limit Levels of Groundwater Quality Monitoring” was submitted to EPD in August 2017. EPD has no further comment on the report and the updated Action and Limit Level is shown in **Appendix A**.

Table 5.6 Summary of Groundwater Quality Monitoring Results

Date	Location	Parameters (unit)								
		pH	Dissolved Oxygen (mg/L)	Turbidity (NTU)	SS (mg/L)	BOD ₅ (mg O ₂ /L)	TOC (mg-TOC/L)	Total Nitrogen (mg/L)	NH ₃ -N (mg NH ₃ -N/L)	Total Phosphorus (mg-P/L)
11 April 2018	Stream 1	7.8	7.8	1.4	3	<2	3	<0.6	<0.05	<0.05
	Stream 2	8.2	7.7	2.0	3	<2	5	0.9	<0.05	<0.05
	Stream 3	N/A*								
24 April 2018	Stream 1	8	7.8	1.6	6.0	<u>4</u>	<u>12</u>	<u>3.7</u>	<0.05	<u>0.06</u>
	Stream 2	8.1	7.8	1.0	6	<u>8</u>	<u>16</u>	<u>2.9</u>	0.07	<u>0.08</u>
	Stream 3	7.9	8	1.4	3.0	<u>4</u>	<u>8</u>	<u>2.9</u>	<u>0.16</u>	<u>0.1</u>
No. of Exceedance	Action Level	0	0	0	0	0	0	0	1	0
	Limit Level	0	0	0	0	3	3	3	0	3

Note: **Bold Italic** means Action Level exceedance

Bold Italic with underline means Limit Level exceedance

Remark*: No groundwater quality monitoring was conducted for Stream 3 on 11 April 2018 due to the drying out of the stream water on that day. The photo record is shown in **Appendix H**.

- 5.36 All groundwater monitoring was conducted as scheduled in the reporting month. One Action Level and Twelve Limit Level exceedances were recorded in the reporting month and drying out of stream water at Stream 3 was observed on 11 April 2018. It is considered that drying out of stream water is non project-related due to no tunnel boring or tunnel construction works in Tseung Kwan O side in this reporting month. And the Action & Limit Level exceedance for groundwater quality recorded on 24 April 2018 is still under investigation and the investigation details will be reported in the next reporting month.

Marine Water Quality Monitoring

- 5.37 All marine water quality monitoring was conducted as scheduled in the reporting month. Marine water monitoring results and graphical presentations are shown in **Appendix I**. Other relevant data was also recorded, such as monitoring location / position, time, sampling depth, weather conditions and any special phenomena or work underway nearby.
- 5.38 Calculated Action and Limit Levels for Marine Water Quality is presented in **Appendix I**. No Action/Limit Level exceedance was recorded in the reporting period.

Groundwater Level Monitoring (Piezometer Monitoring)

- 5.39 Daily piezometer monitoring at any time of the day shall be carried throughout the whole period when any tunnel construction activities are carried out within +/- 50m of the piezometer gate in plan.
- 5.40 No tunnel construction activity carried out within +/- 50m of the piezometer gate. Construction Phase Piezometer Monitoring has not commenced in this reporting period.

6. ECOLOGY

Post-Translocation Coral Monitoring

- 6.1 Post-translocation monitoring survey is recommended in the EM&A Manual to audit the success of coral translocation. Information gathered during each post-translocation monitoring survey should include observations on the presence, survival, health condition and growth of the translocated coral colonies. These parameters should then be compared with the baseline results collected from the pre-translocation survey.
- 6.2 Under Contract No. NE/2015/01 and NE/2015/02, a total of 14 and 29 coral colonies were tagged and translocated respectively from the Donor Site to the Recipient Site in November 2016. Ten (10) corals at the Recipient Site were also tagged by each Contract as reference for post-translocation monitoring.
- 6.3 The post-translocation coral monitoring shall be conducted once every 3 months after completion for a period of 12 months. The fourth post-translocation coral monitoring was carried out on 07 November 2017.
- 6.4 Location of post-translocation coral monitoring is shown in **Figure 7**.

Event and Action Plan

- 6.5 The post-translocation monitoring result was evaluated against Action and Limit Levels presented in **Appendix A**. Evaluation was based on recorded changes in percentage of partial mortality of the corals.
- 6.6 If the defined Action Level or Limit Level for coral monitoring is exceeded, the actions as set out in **Appendix M** will be implemented.
- 6.7 If observations of any die-off / abnormal conditions of the translocated corals are made during the post-translocation monitoring, the ET shall inform the Contractor, IEC and AFCD, and liaise with AFCD to investigate any mitigation measures needed.

Results and Observations

- 6.8 No post-translocation coral monitoring was conducted in the reporting month.
- 6.9 The post-translocation coral monitoring surveys were completed in November 2017.

7. CULTURAL HERITAGE

Monitoring Requirement

- 7.1 According to the EP Conditions and EM&A Manual, monitoring of vibration impacts was conducted when the construction works are less than 100m from the Built Heritage in close proximity of the worksite, namely the Cha Kwo Ling Tin Hau temple. Tilting and settlement monitoring should be applied on the Cha Kwo Ling Tin Hau Temple. Construction works less than 100m from the Cha Kwo Ling Tin Hau temple commenced on 8 April 2017.
- 7.2 As stated in the “*Built Heritage Mitigation Plan*” for this Project, during the period of the construction works conducted within 100m from the Cha Kwo Ling Tin Hau Temple, monitoring on settlement and tilting will be conducted once a day for the Cha Kwo Ling. Monitoring of vibration will be conducted during blasting at Cha Kwo Ling area once a day. When there is no blasting to be conducted at the area, vibration monitoring at the Cha Kwo Ling Tin Hau Temple will be conducted once per day when there are piling works or rock breaking works within the 100m from the Cha Kwo Ling Tin Hau Temple.

Monitoring Locations

- 7.3 One vibration monitoring point and three building settlement monitoring points are proposed for monitoring of the cultural heritage. The building settlement markers are placed on the wall on three sides of the Temple, except the front, of the Cha Kwo Ling Tin Hau Temple and the vibration monitoring point is located within the Cha Kwo Ling Tin Hau Temple. Monitoring Location is shown in **Figure 8**.

Monitoring Equipment

- 7.4 Building settlement is measured via a settlement marker attached to the wall of Cha Kwo Ling Tin Hau Temple by adhesive tape.
- 7.5 Vibration monitoring was conducted by using vibrographs: Minimate Plus manufactured by InstanTel. These vibrographs will be calibrated annually and its performance follows the requirements given in the “*Guidance Note on Vibration Monitoring*” (GN-VM) issued by the Civil Engineering and Development Department, which is based on the Performance Specification for Blasting Seismographs by International Society of Explosive Engineers (ISEE (2000)).
- 7.6 **Table 7.1** summarizes the equipment employed by the Contractor for cultural heritage monitoring. Copies of calibration certificates are attached in **Appendix B**.

Table 7.1 Cultural Heritage Monitoring Equipment

Equipment	Manufacturer and Model	Quantity
Digital Level for tilting	Leica Serial No.: 701133	1
iCivil-1011 Inclinometer for building settlement	iCivil-1011 Inclinometer Serial No.: HK110118 / HK110120	2
Vibrographs for vibration monitoring	MiniMate Plus manufactured by InstanTel Model No.: 716A0403	3

Monitoring Methodology

- 7.7 Vibrograph (velocity seismograph) was deployed at each monitoring station to

measure and record the PPV and amplitude of ground motion in three mutually perpendicular directions. Vibration monitoring equipment fulfils the requirements stated in the Government guidelines and is calibrated to HOKLAS standards. Each monitoring would not be more than 10 minutes. Settlement monitoring should be conducted by surveyors manually.

Alert, Alarm and Action Levels

- 7.8 The Alert, Alarm and Action (AAA) Levels are given in **Table 7.2**.

Table 7.2 AAA Levels for Monitoring for Cultural Heritage

Parameter	Alert Level	Alarm Level	Action Level
Vibration	ppv: 4.5 mm/s	ppv: 4.8 mm/s	ppv: 5mm/s Maximum Allowable Vibration Amplitude: 0.1mm
Building Settlement Markers	6mm	8mm	10mm
Building Tilting ⁽¹⁾	1:2000	1:1500	1:1000

Remarks: (1) Building tilting measurement was replaced by building settlement point measurement. The tilting can be calculated by the ratio of the maximum settlement difference between 2 points and the distance between the 2 points.

Results

- 7.9 In the reporting month, cultural heritage monitoring was carried out by the Contractor at the aforesaid location on 23 occasions. No AAA Level exceedance was recorded in the reporting month. The monitoring results are presented in **Appendix T**.

Mitigation Measures for Cultural Heritage

- 7.10 According to Condition 3.6 of the EP (EP No.: EP-458/2013/C), to prevent damage to Cha Kwo Ling Tin Hau Temple and its Fung Shui rocks (Child-given rocks) during the construction phase, a temporarily fenced-off buffer zone (Rocks buffer zone is 5 m from the edge of Rocks and 15m from the edge of Rocks alter) with allowance for public access (minimum 1 m) around the temple and the Fung Shui rocks shall be provided. The open yard in front of the temple should be kept as usual for annual Tin Hau festival.
- 7.11 As there is a large buffer distance from the current works to Cha Kwo Ling Tin Hau Temple and the Fung Shui rocks (Child-given rocks), the temporarily fenced-off rocks buffer zone and from the edge of Rocks alter is not required. The fenced-off rocks buffer zone would be implemented when there is construction activities in vicinity of the cultural heritage.

8. LANDSCAPE AND VISUAL IMPACT REQUIREMENTS

- 8.1 Landscape and visual mitigation measures during the construction phase shall be checked to ensure that they are fully realized and implemented on site.
- 8.2 Site audits were carried out on a weekly basis to monitor and audit the timely implementation of landscape and visual mitigation measures listed in “Implementation Schedule and Recommended Mitigation Measures” (shown in **Appendix N**). The summaries of observations and recommendations related to landscape and visual impacts, if any, are shown in **Appendix L**.
- 8.3 No non-compliance of the landscape and visual impact was recorded in the reporting month.

9. LANDFILL GAS MONITORING**Monitoring Requirement**

- 9.1 In accordance with the EM&A Manual, monitoring of landfill gas is required for construction works within the Sai Tso Wan Landfill Consultation Zone during the construction phase. This section presents the results of landfill gas measurements performed by the Contractor. **Appendix A** shows the Limit Levels for the monitoring works.
- 9.2 The “Landfill Gas Monitoring Proposal”, including the monitoring programme and detailed actions, is submitted to the EPD for approval. Details of monitoring in this Proposal is in line with the monitoring requirements stipulated in the EM&A Manual.

Monitoring Parameters and Frequency

- 9.3 Monitoring parameters for Landfill gas monitoring include Methane, Carbon dioxide and Oxygen.
- 9.4 According to the implementation schedule and recommended mitigation measures of the EM&A Manual, measurements of the following frequencies should be carried out:

Excavations deeper than 1m

- at the ground surface before excavation commences;-
- immediately before any worker enters the excavation;
- at the beginning of each working day for the entire period the excavation remains open; and
- periodically throughout the working day whilst workers are in the excavation.

Excavations between 300mm and 1m deep

- directly after the excavation has been completed; and
- periodically whilst the excavation remains open.

For excavations less than 300mm deep

- monitoring may be omitted, at the discretion of the Safety Officer or other appropriately qualified person

Monitoring Locations

- 9.5 Monitoring of oxygen, methane and carbon dioxide was performed for excavations at 1m depth or more within the Consultation Zone. In this reporting month, the area required to be monitored for landfill gas are shown below and **Figure 6** shows the landfill gas monitoring locations.
- | | |
|-----------------------------------|-------------|
| ➤ Excavation Locations: | Portion III |
| ➤ Manholes and Chambers: | N/A |
| ➤ Relocation of monitoring wells: | N/A |
| ➤ Any other Confined Spaces: | N/A |

Monitoring Equipment

- 9.6 **Table 9.1** summarizes the equipment employed by the Contractor for the landfill gas monitoring.

Table 9.1 Landfill Gas Monitoring Equipment

Equipment	Model and Make	Quantity
Portable gas detector	ALTAIR 5X Multigas Detector (Serial No. 120848)	1

Results and Observations

- 9.7 In the reporting month, landfill gas monitoring was carried out by the Contractor at the aforesaid locations on 46 occasions. No Limit Level exceedance for landfill gas monitoring was recorded in the reporting month. The monitoring results are provided in **Appendix R**. Copies of calibration certificates are attached in **Appendix B**.

10. ENVIRONMENTAL AUDIT**Site Audits**

- 10.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix L**.
- 10.2 Joint weekly site audits by the representatives of the Engineer, Contractor and the ET were conducted in the reporting month as shown in below:
- Contract No. NE/2015/01: 4, 11, 18 and 25 April 2018
 - Contract No. NE/2015/02: 6, 12, 17 and 26 April 2018
 - Contract No. NE/2015/03: 6, 11, 20 and 27 April 2018
 - Contract No. NE/2017/01: 24 April 2018
 - Contract No. NE/2017/02: 4, 9, 16, 23 and 30 April 2018
- Monthly joint site inspection with the representative of IEC was conducted for NE/2015/01, NE/2015/02, NE/2015/03, NE/2017/01 and NE/2017/02 on 25, 26, 11, 24, 16 April 2018 respectively. EPD has joined the site inspection on 26 April 2018.

Implementation Status of Environmental Mitigation Measures

- 10.3 According to the EIA Study Report, Environmental Permit and the EM&A Manual of the Project, the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An updated summary of the Implementation Schedule and Recommended Mitigation Measures is provided in **Appendix N**.
- 10.4 During site inspections in the reporting month, no non-compliance was identified. The observations and recommendations made during the audit sessions are summarized in **Appendix L**.
- 10.5 Further to the observations summarized in **Appendix L**, EPD has also identified the following observations during the inspection for Contract No. NE/2015/02 on 26 April 2018:
- Dense white fume emitted from marine vessels on-site
 - Door of the engine of dredger was not closed properly

11. WASTE MANAGEMENT

- 11.1 Waste generated from this Project includes inert construction and demolition (C&D) materials, non-inert C&D materials and marine sediments. Inert C&D waste includes soil, broken rock, broken concrete and building debris, while non-inert C&D materials are made up of C&D waste which cannot be reused or recycled and has to be disposed of at the designated landfill sites. Marine sediment shall be expected from excavation and dredging works of this Project.
- 11.2 With reference to relevant handling records of this Project, the quantities of different types of waste generated in the reporting month are summarised and presented in **Appendix P**.
- 11.3 The Contractors are advised to minimize the wastes generated through the recycling or reusing. All mitigation measures stipulated in the approved EM&A Manual and waste management plans shall be fully implemented. The status of implementation of waste management and reduction measures are summited in **Appendix N**.

12. ENVIRONMENTAL NON-CONFORMANCE**Summary of Exceedances**

- 12.1 Thirteen (13) Action Level exceedances for noise monitoring were recorded due to the documented complaints received in this reporting month.
- 12.2 One Action Level and Twelve Limit Level exceedances for groundwater quality monitoring were recorded in the reporting month.
- 12.3 Actions carried out in accordance with the Event and Action Plans in **Appendix M** are presented in **Appendix K – Summary of Exceedance**.

Summary of Environmental Non-Compliance

- 12.4 No environmental non-compliance was recorded in the reporting month.

Summary of Environmental Complaint

- 12.5 Fourteen (14) environmental complaints were received in the reporting month. The Cumulative Complaint Log is presented in **Appendix O**. The investigation status and result is also reported in **Appendix O**.

Summary of Environmental Summon and Successful Prosecution

- 12.6 No notification of summon or successful environmental prosecution was received in this reporting period. The Cumulative Log for environmental summon and successful prosecution since the commencement of the Project is presented in **Appendix O**.

13. FUTURE KEY ISSUES

13.1 Tentative construction programmes for the next three months are provided in **Appendix Q**.

13.2 Major site activities to be undertaken for the next reporting period are summarized in **Table 13.1**.

Table 13.1 Summary Table for Site Activities in the next Reporting Period

Contract No.	Project Title	Site Activities (May 2018)	
NE/2015/01	Tseung Kwan O – Lam Tin Tunnel – Main Tunnel and Associated Works	Lam Tin Interchange	1. EHC2 U-Trough 2. Site Formation – Area 1G1, Area 1G2, Area 2 , Area 3, Area 4 & Area 5
		Main Tunnel	1. Main tunnel Excavation
		TKO Interchange	1. Haul Road Construction, Site Formation and Slope Works 2. Steel Platform for Bridge Construction
NE/2015/02	Tseung Kwan O – Lam Tin Tunnel – Road P2 and Associated Works	1. Pre-bored works, sheet piling and interlocking pipe piles installation works at Portion IV & VII 2. Removal of existing seawall blocks at Portion IV & VII 3. Reconstruction of existing outfall and installation of DN2100 drainage system at Portion IV & VII 4. Pre-bored works at Portion V & VI 5. Waterproofing, backfilling works and wall construction at Portion VIII 6. Dredging at Portion IX 7. Seawall Construction at Portion IX 8. Placing sand blanket at non-dredged area at Portion IX	
NE/2015/03	Tseung Kwan O – Lam Tin Tunnel – Northern Footbridge	1. Construction of Pile Cap PC4 and Sump Pit 2. Install steel mould for main deck	
NE/2017/01	Tseung Kwan O Interchange and Associated Works	1) Construction of Site Office 2) Erection of Temporary platform for pre-drill and bore pile work 3) Ground Investigation Works	
NE/2017/02	Tseung Kwan O - Lam Tin Tunnel - Road P2/D4 and Associated Works	1) Trial pit 2) Underground utilities detection 3) Temporary traffic arrangement Setup 4) Site office erection 5) Communication Liaison Center erection 6) Modification of traffic island 7) Fencing erection 8) Predrilling 9) Construction of drainage and watermain	

Key Issues for the Coming Month

13.3 Key environmental issues in the coming month include:

- Watering for dust generation from haul road, stockpiles of dusty materials, exposed site area, excavation works and rock breaking activities;
- Noisy construction activity such as rock-breaking activities and piling works;
- Runoff from exposed slope or site area;
- Wastewater and runoff discharge from site;
- Accumulation of silt, mud and sand along U-channels and sedimentation tanks;
- Set up and implementation of temporary drainage system for the surface runoff;
- Storage of chemicals/fuel and chemical waste/waste oil on site;
- Accumulation and storage of general and construction waste on site; and
- Marine water quality impact and indirect impact to coral communities due to marine construction for TKO-LTT reclamation.

Monitoring Schedule for the Next Month

13.4 The tentative environmental monitoring schedules for the next month are shown in **Appendix D**.

14. CONCLUSIONS AND RECOMMENDATIONS**Conclusions**

- 14.1 This is the 18th Environmental Monitoring and Audit (EM&A) Report which presents the EM&A works undertaken during the period in April 2018 in accordance with EM&A Manual and the requirement under EP.

Air Quality Monitoring

- 14.2 All 1-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.
- 14.3 All 24-hour TSP monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

Construction Noise Monitoring

- 14.4 All noise monitoring was conducted as scheduled in the reporting month. Thirteen (13) Action Level exceedance was recorded due to the documented complaints received in this reporting month. No Limit Level exceedance was recorded in the reporting month.

Water Quality Monitoring

- 14.5 Groundwater monitoring was conducted as scheduled in the reporting month. One Action Level and Twelve Limit Level exceedances were recorded in the reporting month.
- 14.6 All marine water monitoring was conducted as scheduled in the reporting month. No Action/Limit Level exceedance was recorded.

Ecological Monitoring

- 14.7 The post-translocation coral monitoring surveys were completed in November 2017.

Monitoring on Cultural Heritage

- 14.8 No Alert Alarm and Action (AAA) Level exceedance of cultural heritage monitoring on cultural heritage was recorded in the reporting month.

Landscape and Visual Monitoring and Audit

- 14.9 No non-compliance of the landscape and visual impact was recorded in the reporting month.

Landfill Gas Monitoring

- 14.10 Monitoring of landfill gases in the reporting month was carried out by the Contractor at excavation location, Portion III. No Limit Level exceedance was recorded.

Environmental Site Inspection

- 14.11 Joint weekly site inspections were conducted by representatives of the Contractor, Engineer and Environmental Team. During site inspections in the reporting month, no non-compliance was identified but environmental deficiency was observed. The environmental deficiency observed during the reporting month are shown in **Appendix L**.

Complaint, Prosecution and Notification of Summons

- 14.12 Fourteen (14) environmental complaints, no successful prosecution and notification of summon were received during the reporting period.

Recommendations

- 14.13 The following recommendations were made to the Contractor for the reporting month:

Air Quality Impact

- To implement dust suppression measures such as water spray on all haul roads, stockpiles, dry surfaces and open slopes.
- To cover stockpile of dusty material by impervious material.
- To avoid dark smoke emitted from the generator.

Construction Noise

- To provide noise mitigation measures (e.g. Temporary noise barrier or Full enclosure) to PME as proposed in the approved Noise Mitigation Plan.
- To repair the gaps between the noise barriers.

Water Quality Impact

- To provide and repair the silt curtain to fully enclose the site and prevent any gap between the silt curtains.
- To review and implement temporary drainage system.
- To clear the litter, debris, silt and sediment in drainage or catchpits.
- To remove the sand or dusty material deposited near the seafront.
- To provide bund or covers to gullies and stockpile storage area on site to avoid leakage of surface runoff.
- To divert all the water generated from construction site to de-silting facilities with enough handling capacity before discharge.
- To maintain the sedimentation tank more frequently to ensure proper wastewater treatment before discharge.


Waste/Chemical Management

- To remove construction waste regularly.
- To avoid any discharge or accidental spillage of chemical waste or oil directly from the equipment.
- To provide drip tray to chemical containers to avoid any chemical leakage.
- To remove the oil stain and disposed of as chemical waste.
- To remove the stagnant water regularly found inside the drip tray.

Landscape and Visual

- To set up proper tree protection area.
- To avoid placing any construction materials in the tree protection zone.

FIGURES

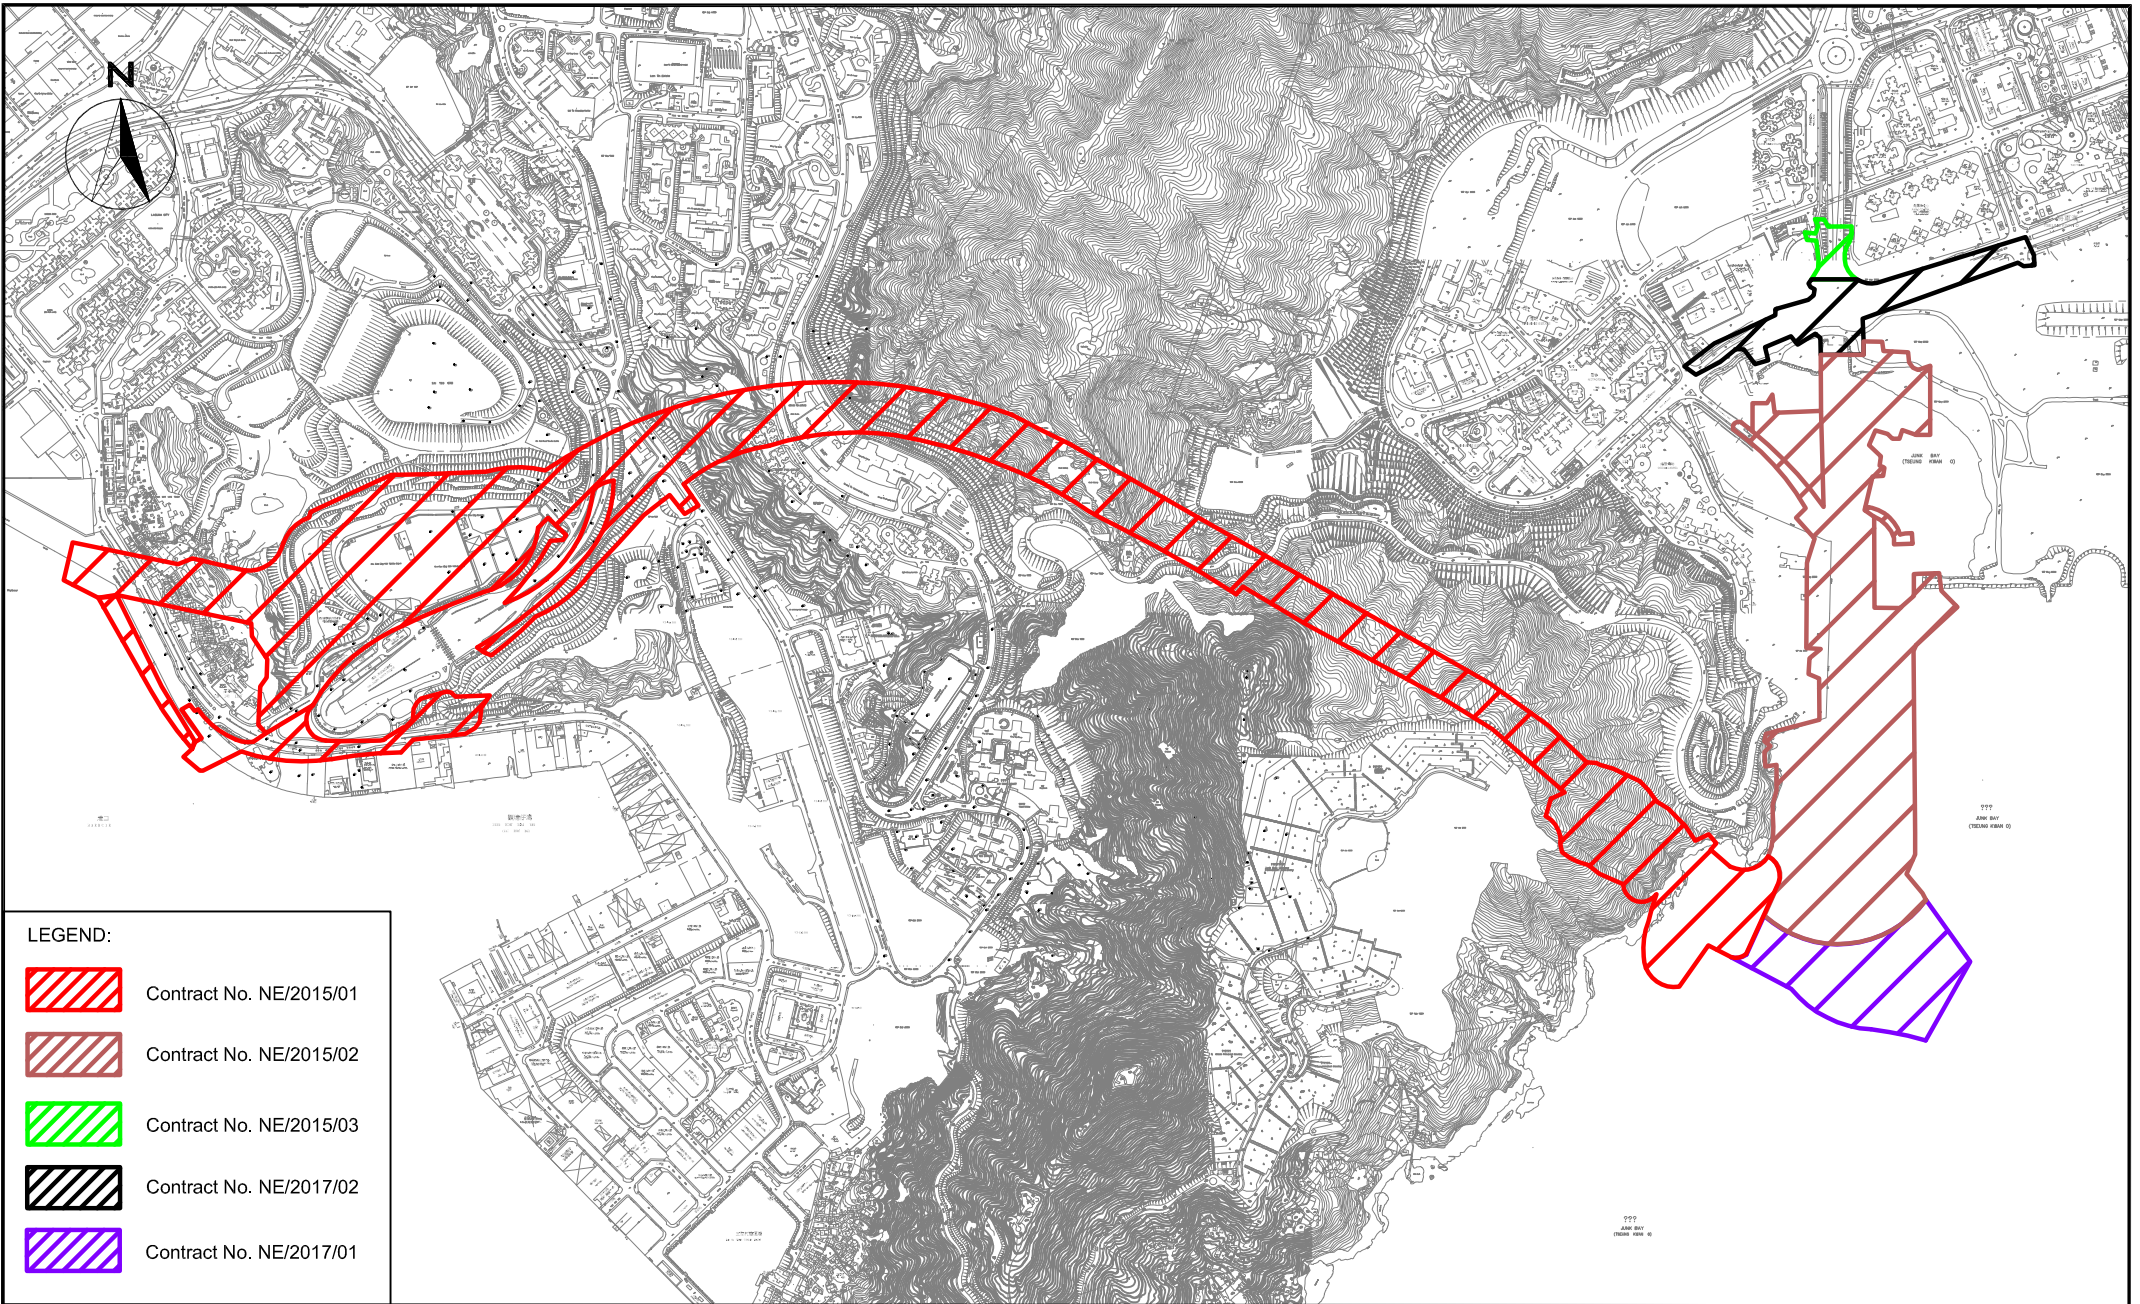


LEGEND:

	Contract No. NE/2015/01
	Contract No. NE/2015/02
	Contract No. NE/2015/03
	Contract No. NE/2017/02
	Contract No. NE/2017/01


CINOTECH
Cinotech Consultants Limited

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel
- Design and Construction
Site Layout Plan


SCALE	1:15000 @ A4	DATE	APR 2018
CHECK	JF	DRAWN	AC
JOB No.	MA16034	FIGURE NO.	1
		REV	-

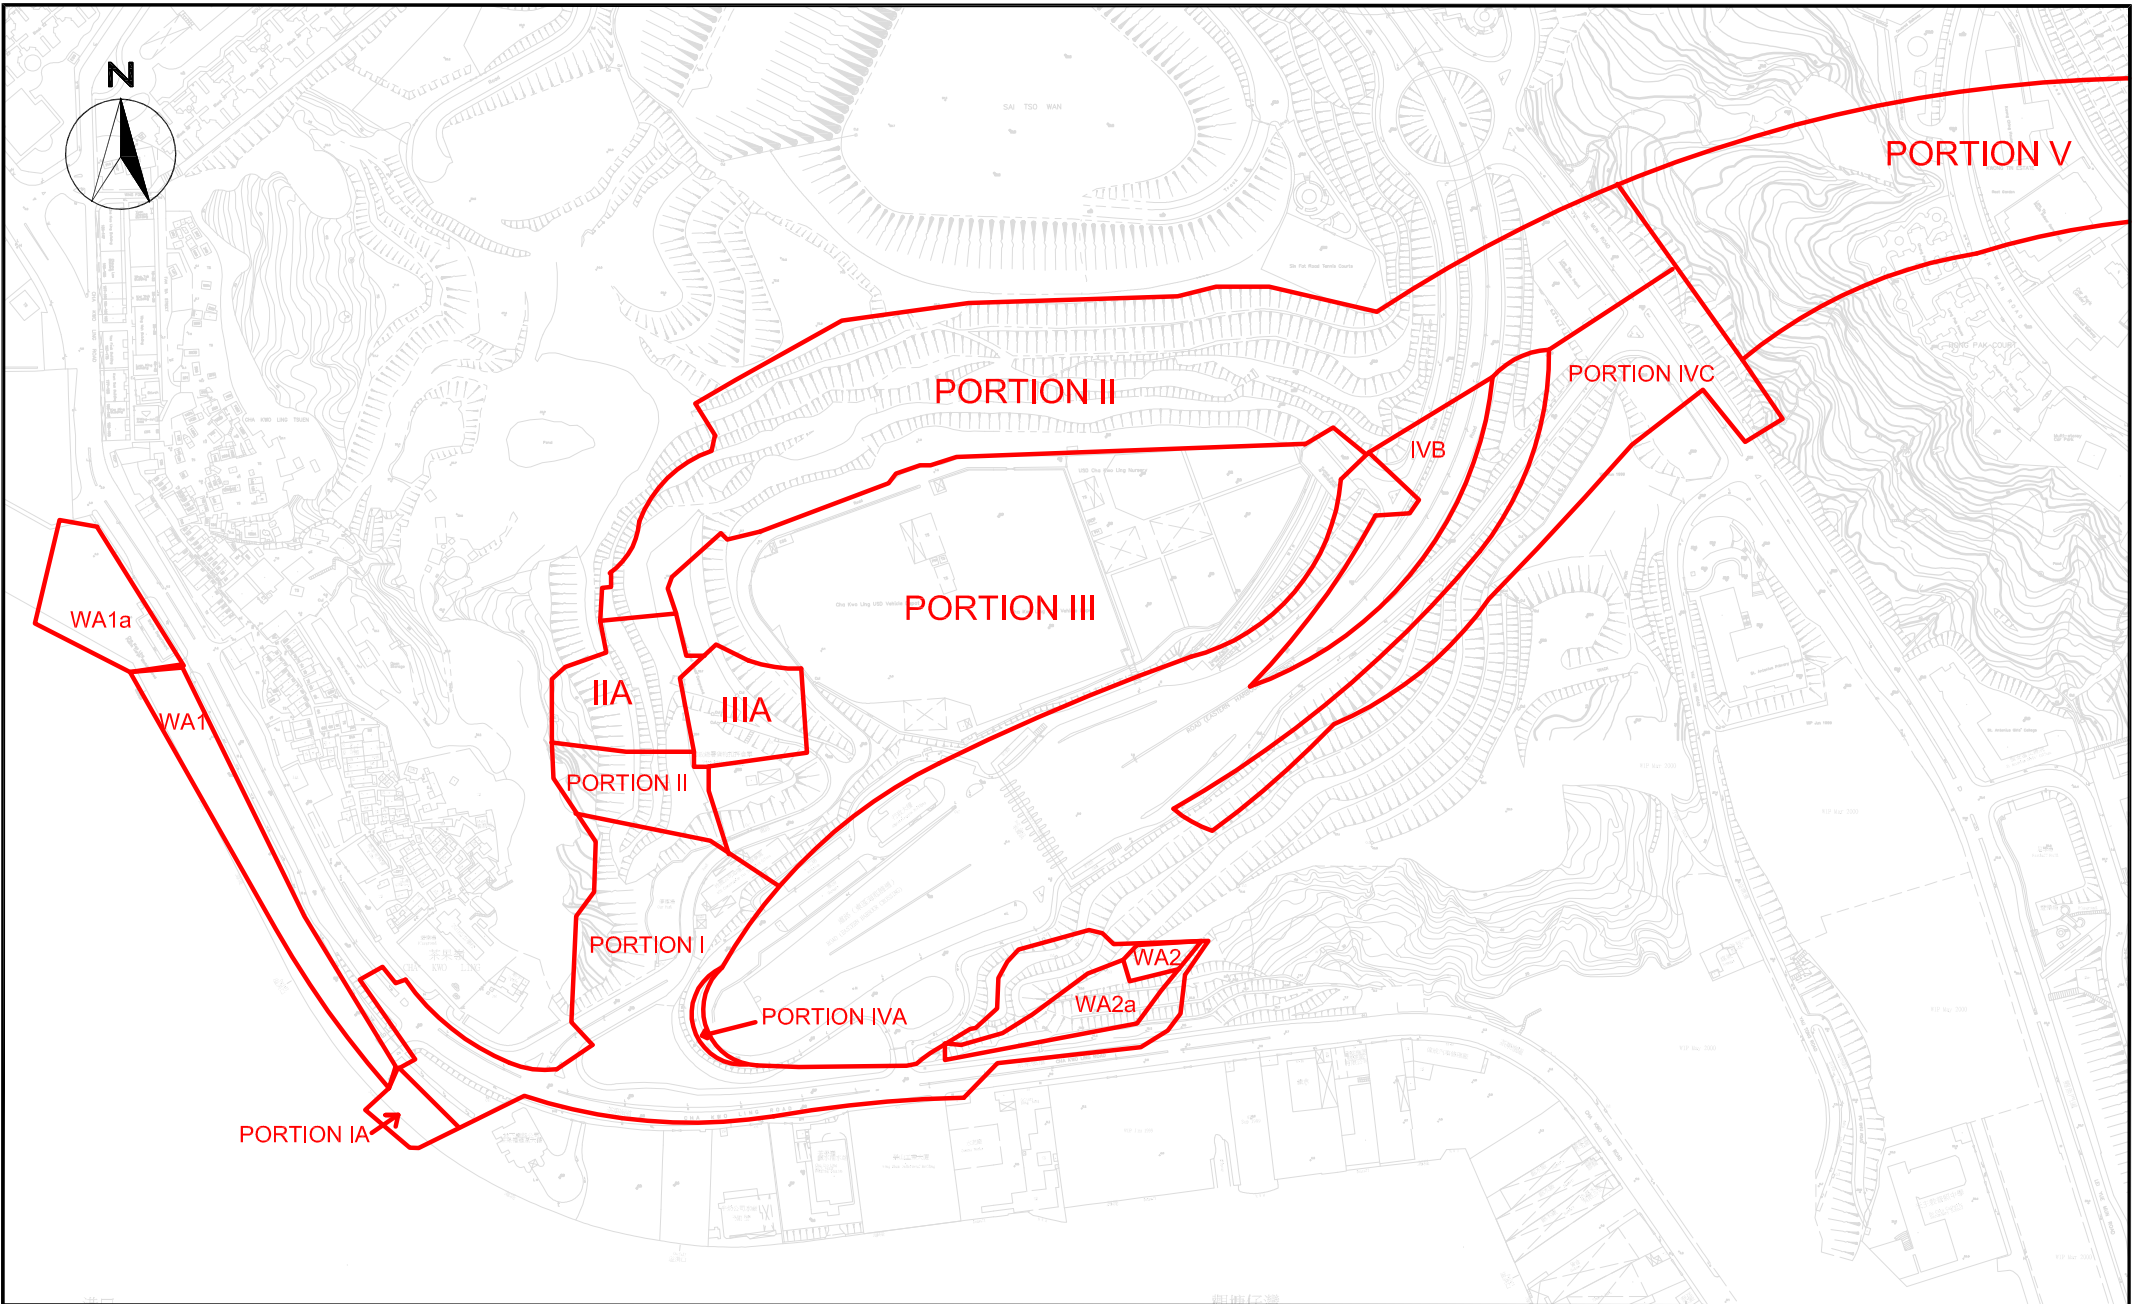


SCALE	1:15000 @ A4	DATE	JAN 2018	
CHECK	JF	DRAWN	JW	
JOB No.	MA16034	FIGURE NO.	1a	REV -

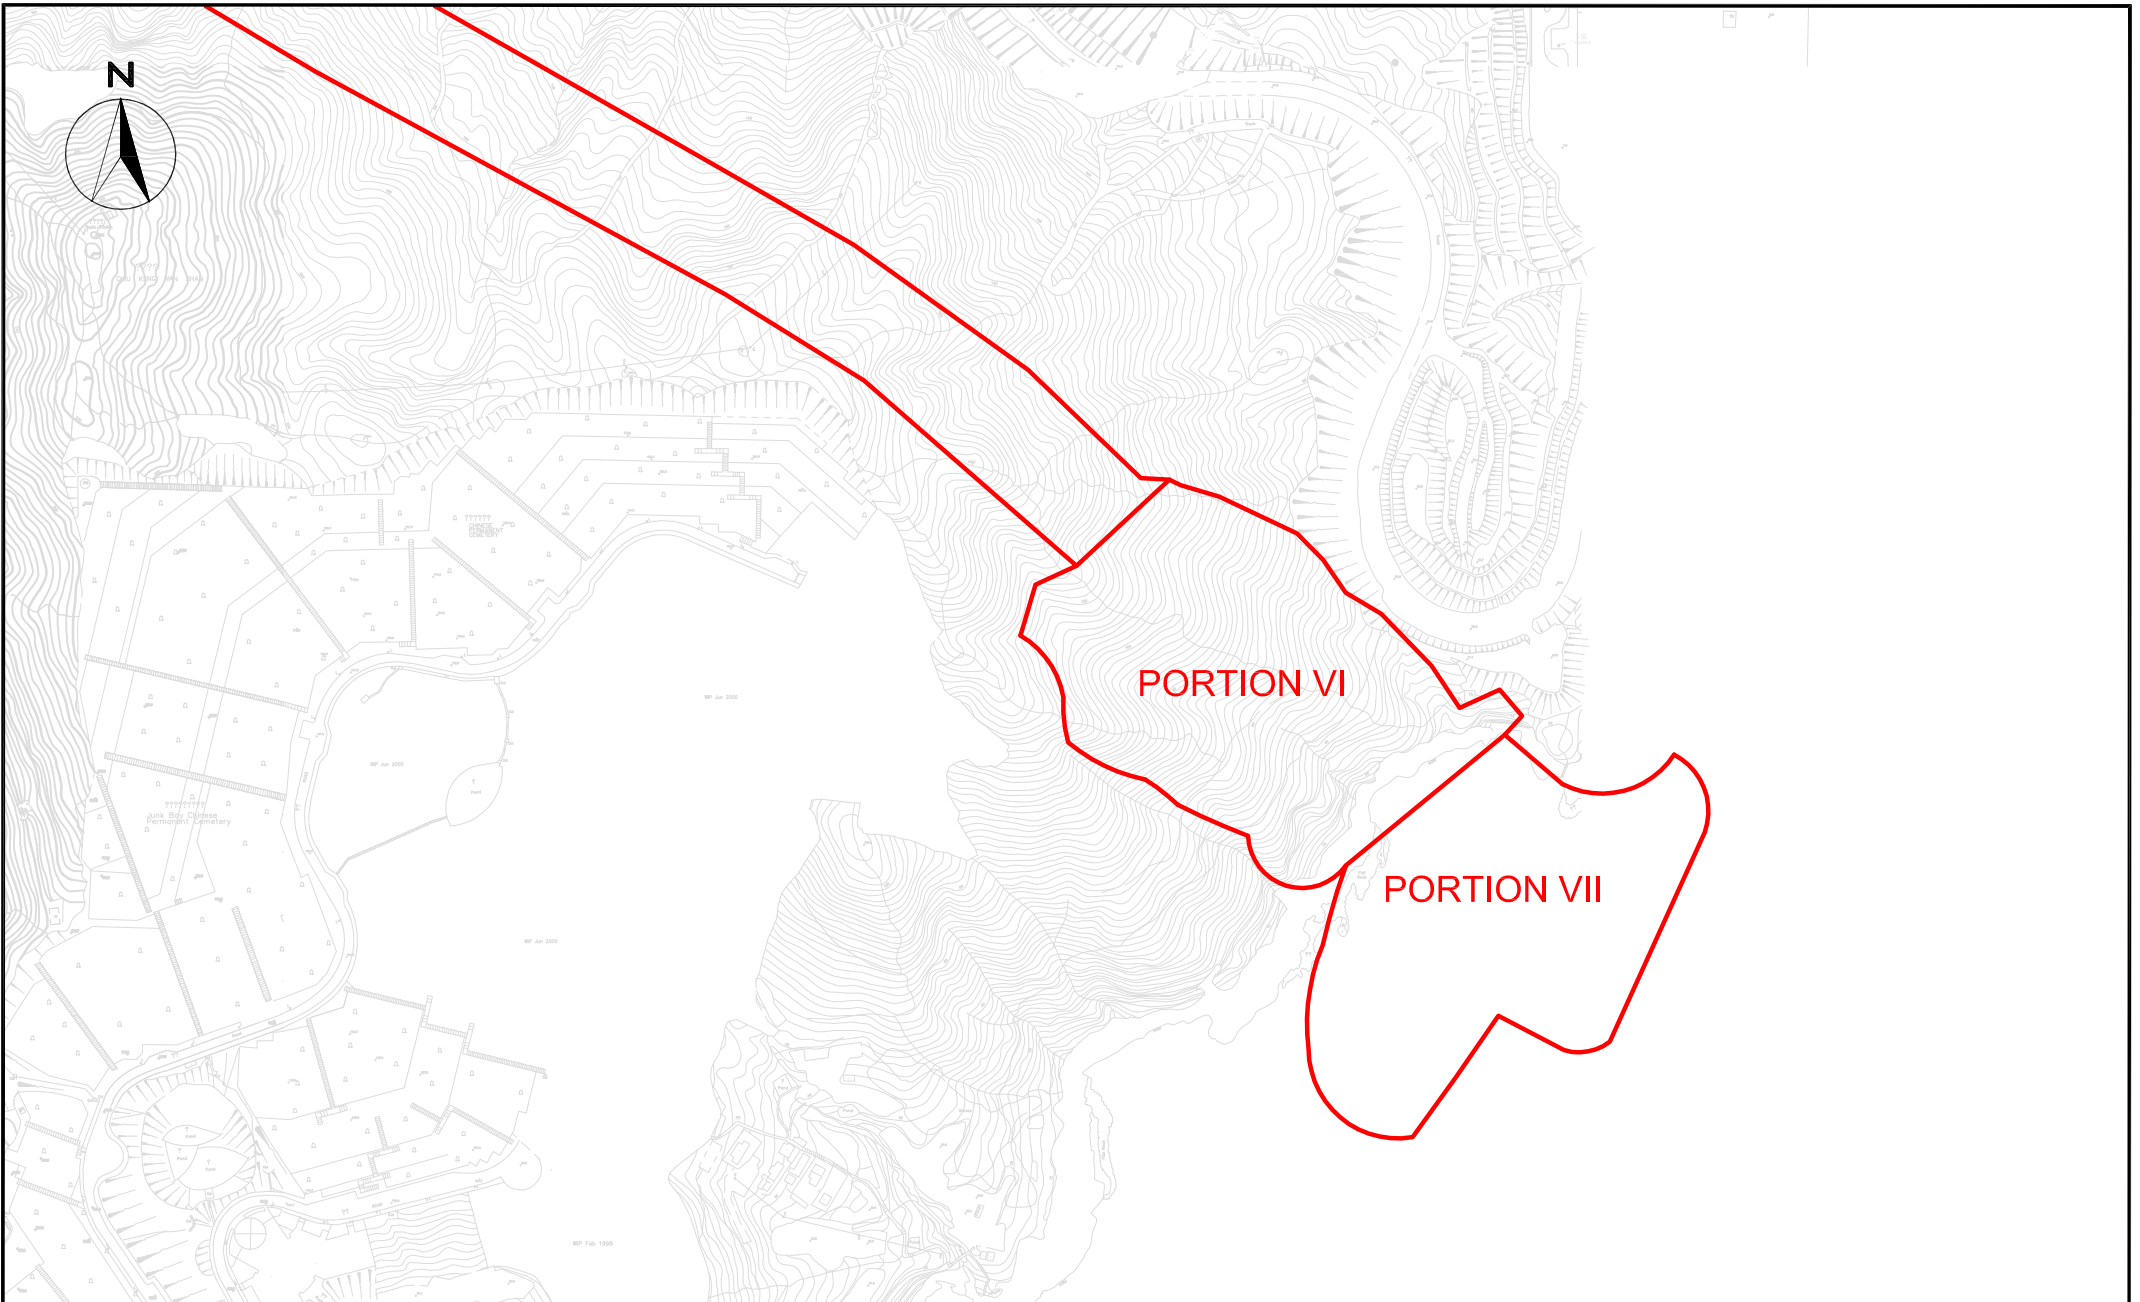

SCALE	1:15000 @ A4	DATE	JAN 2018	
CHECK	JF	DRAWN	JW	
JOB No.	MA16034	FIGURE NO.	1b	REV -

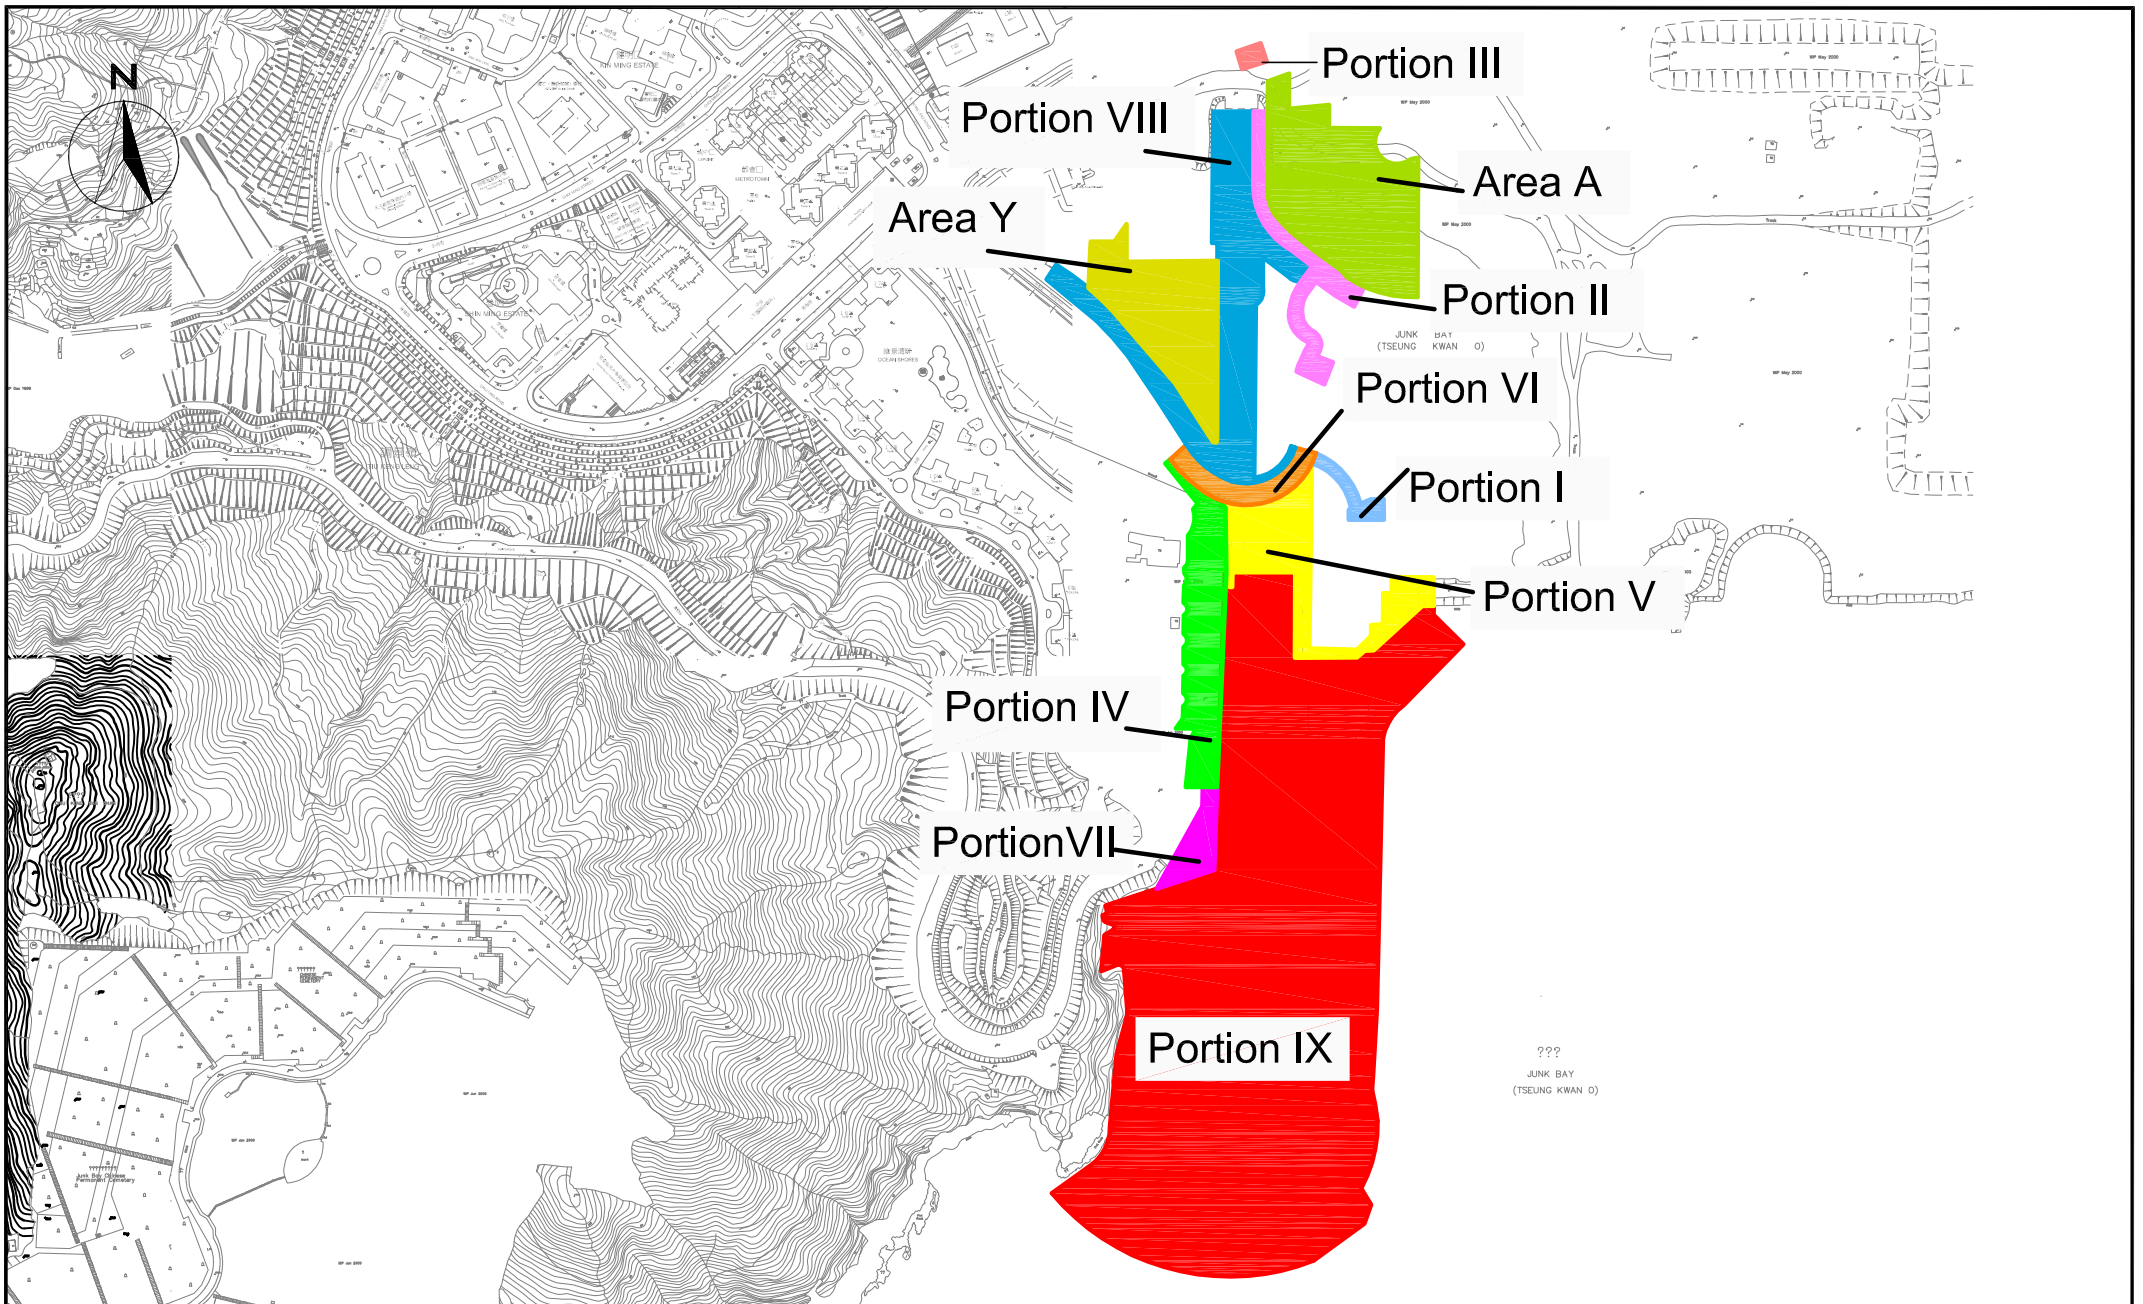


SCALE	N.T.S.	DATE	AUG 2017	
CHECK	JF	DRAWN	JW	
JOB No.	MA16034	FIGURE NO.	1c	REV -

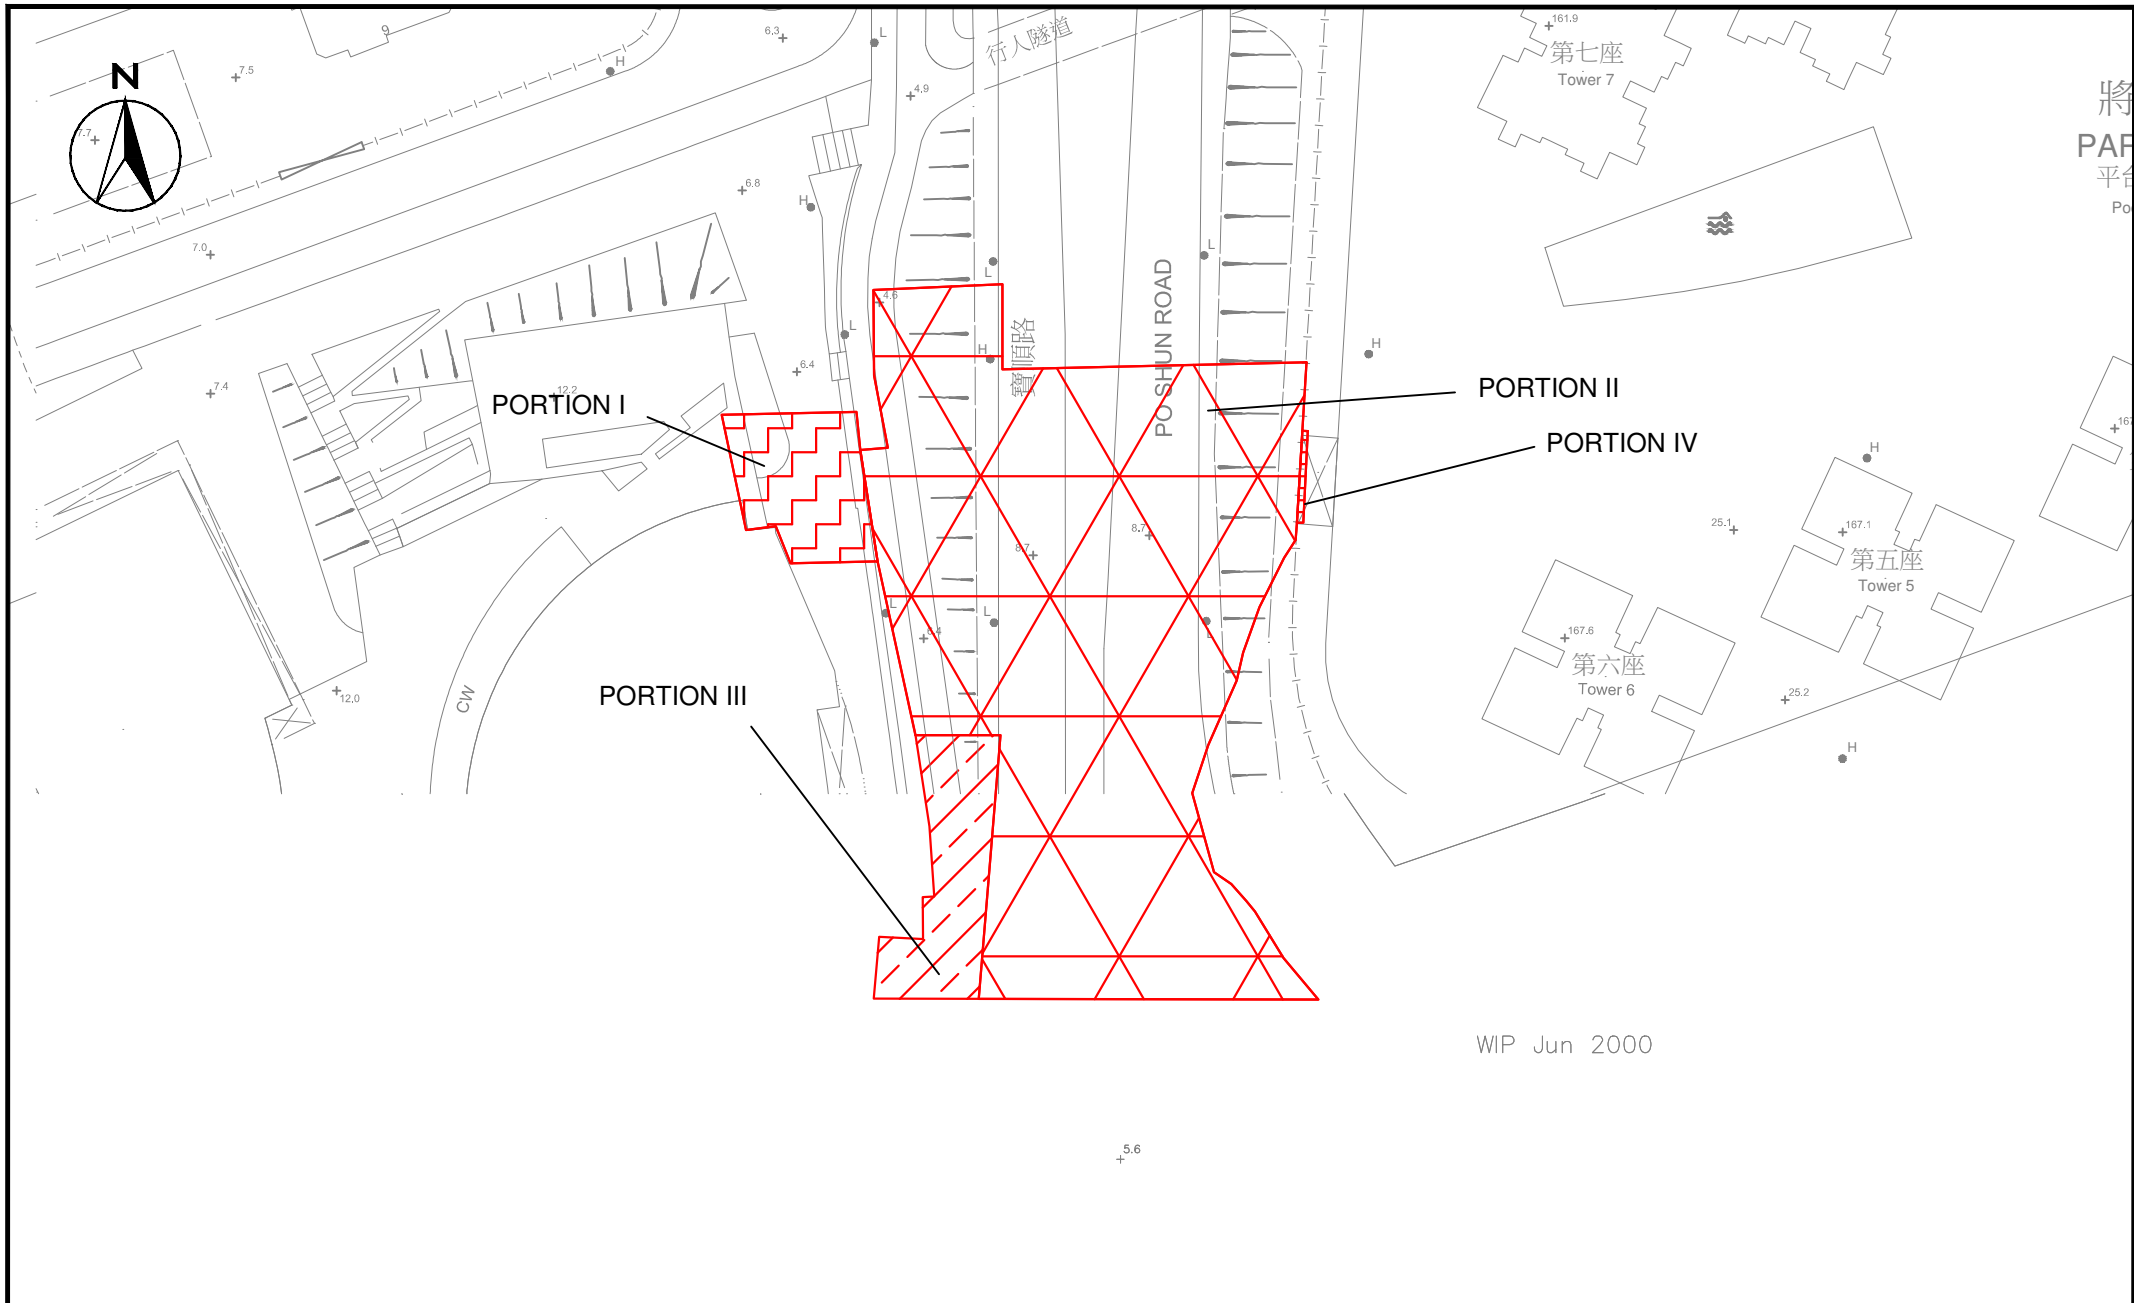

WIP Jun 2000


SCALE	1:2500 @ A4	DATE	JUN 2018	
CHECK	VC	DRAWN	AC	
JOB No.	MA16034	FIGURE NO.	1d	REV
				-

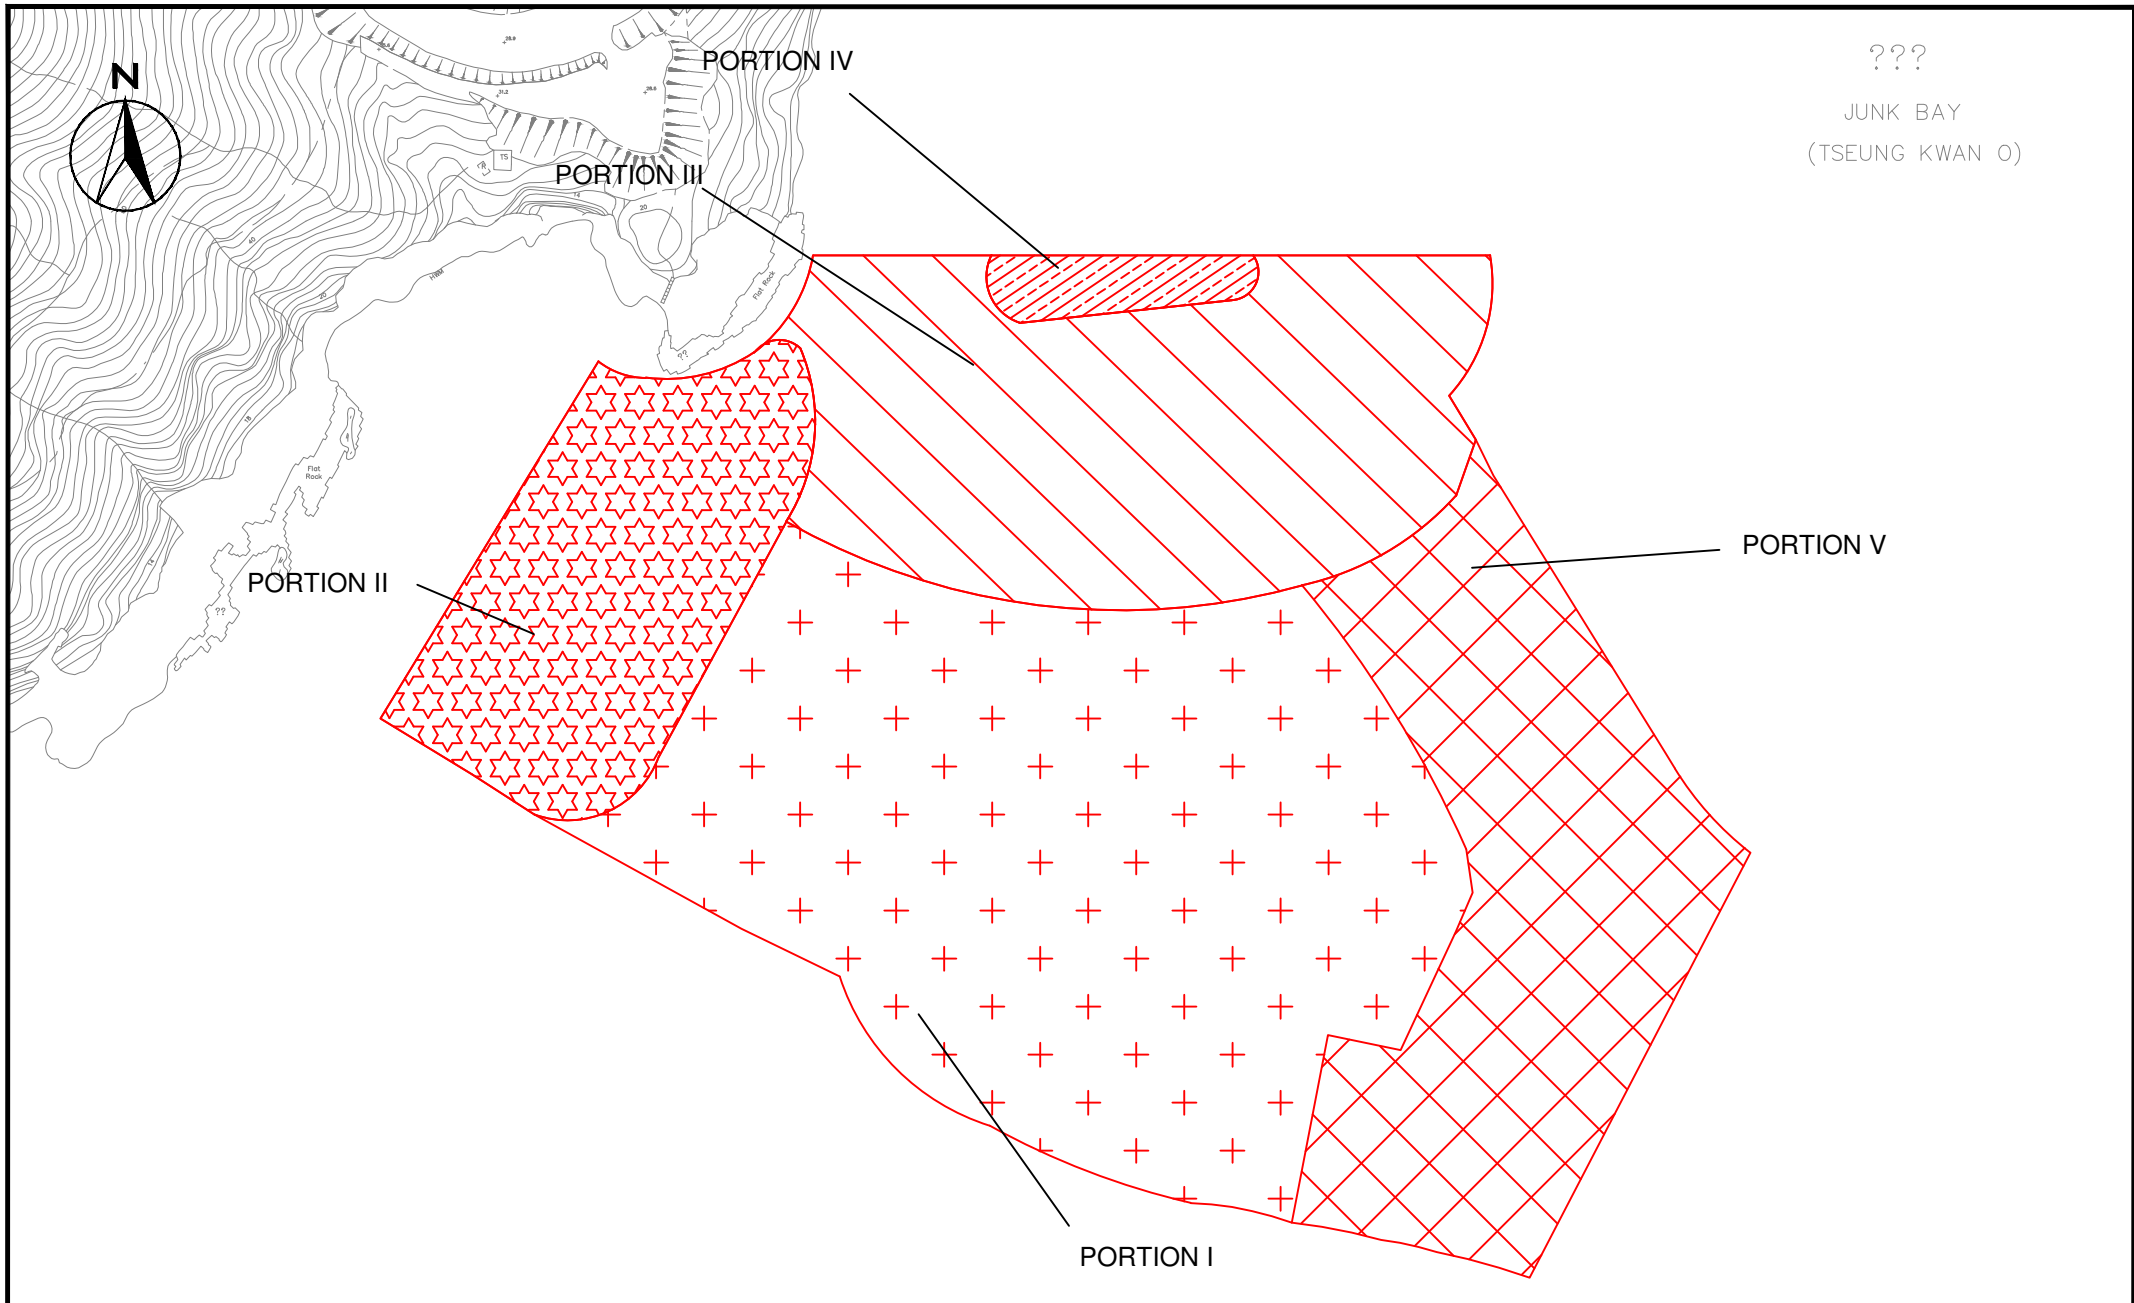


???

JUNK BAY
(TSEUNG KWAN O)

SCALE	1:2500 @ A4	DATE	JUN 2018	
CHECK	VC	DRAWN	AC	
JOB No.	MA16034	FIGURE NO.	1e	REV
				-

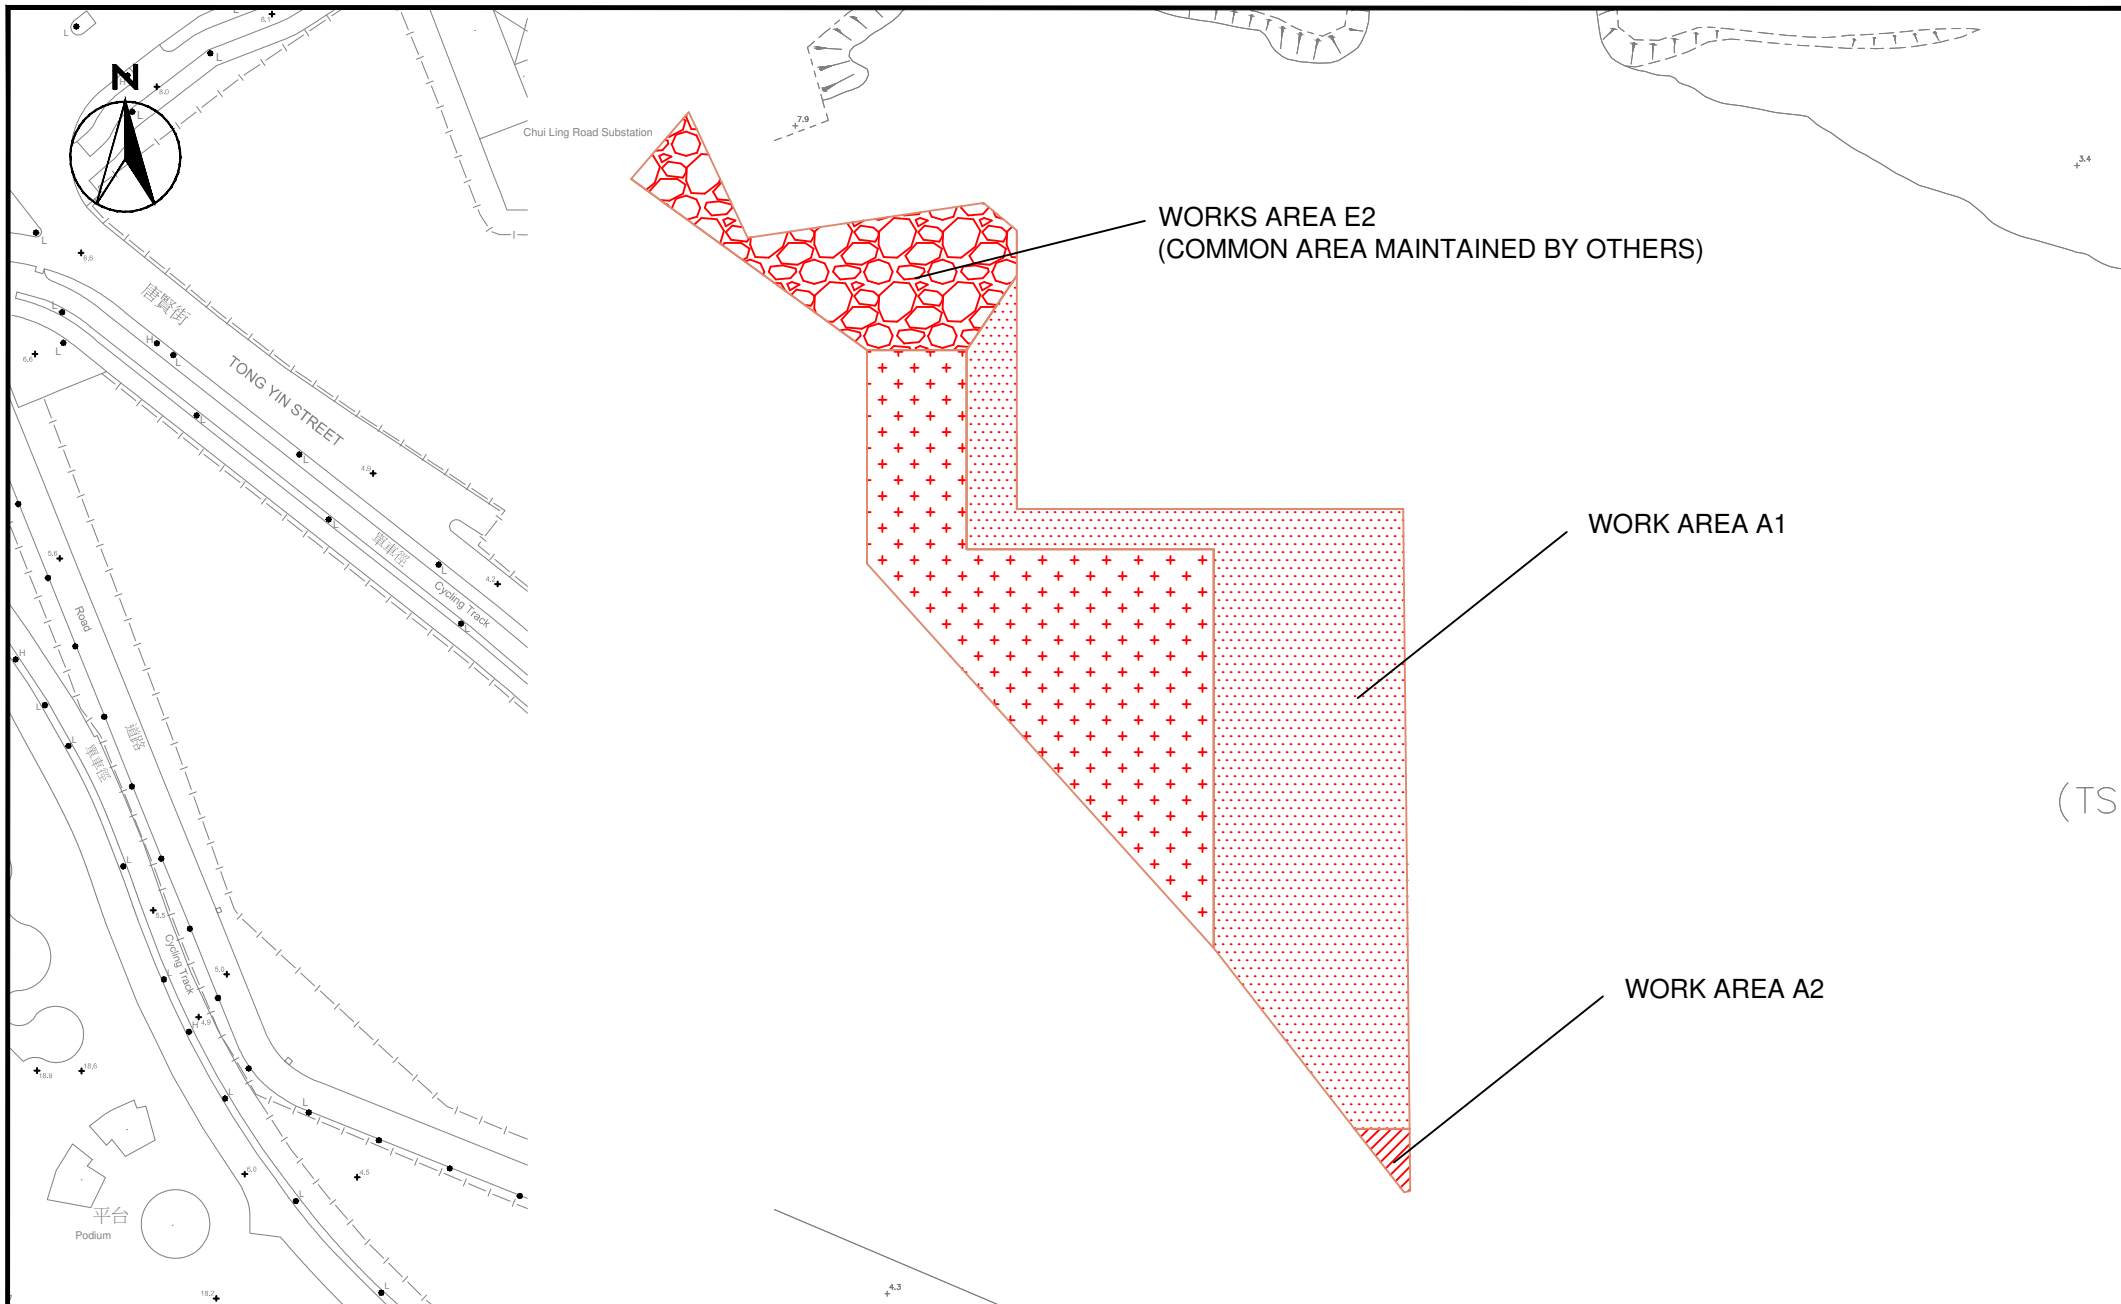


SCALE	1:1500 @ A4	DATE	JUN 2018	
CHECK	VC	DRAWN	AC	
JOB No.	MA16034	FIGURE NO.	1f	REV
				-

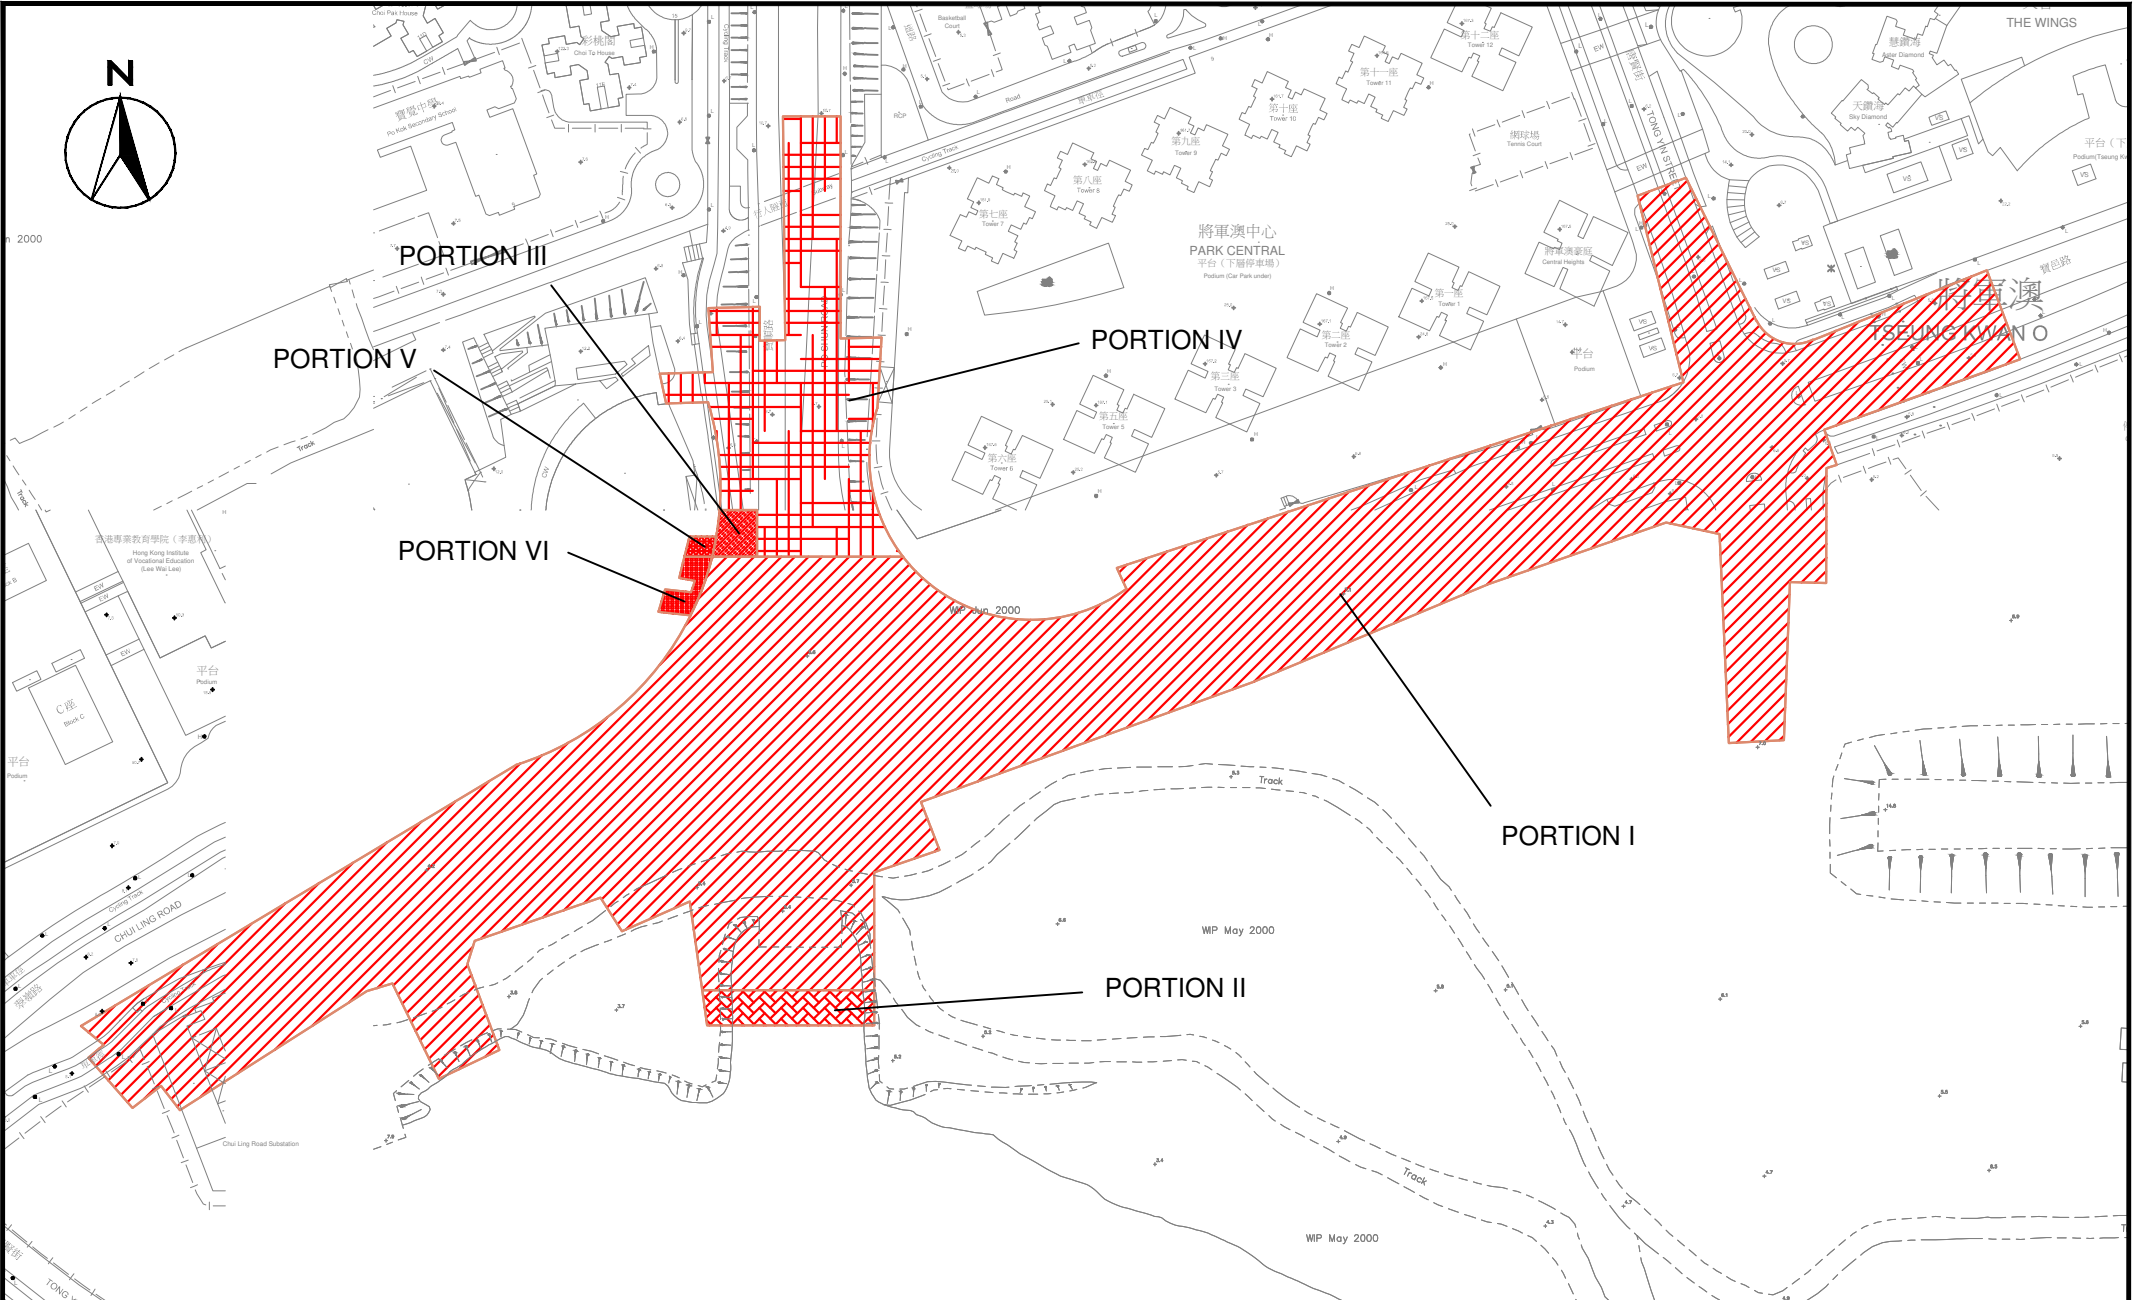


Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel
 - Design and Construction
 Site Portions under Work Contract No. NE/2017/02

SCALE	1:2500 @ A4	DATE	JUN 2018	
CHECK	VC	DRAWN	AC	
JOB No.	MA16034	FIGURE NO.	1g	REV
				-

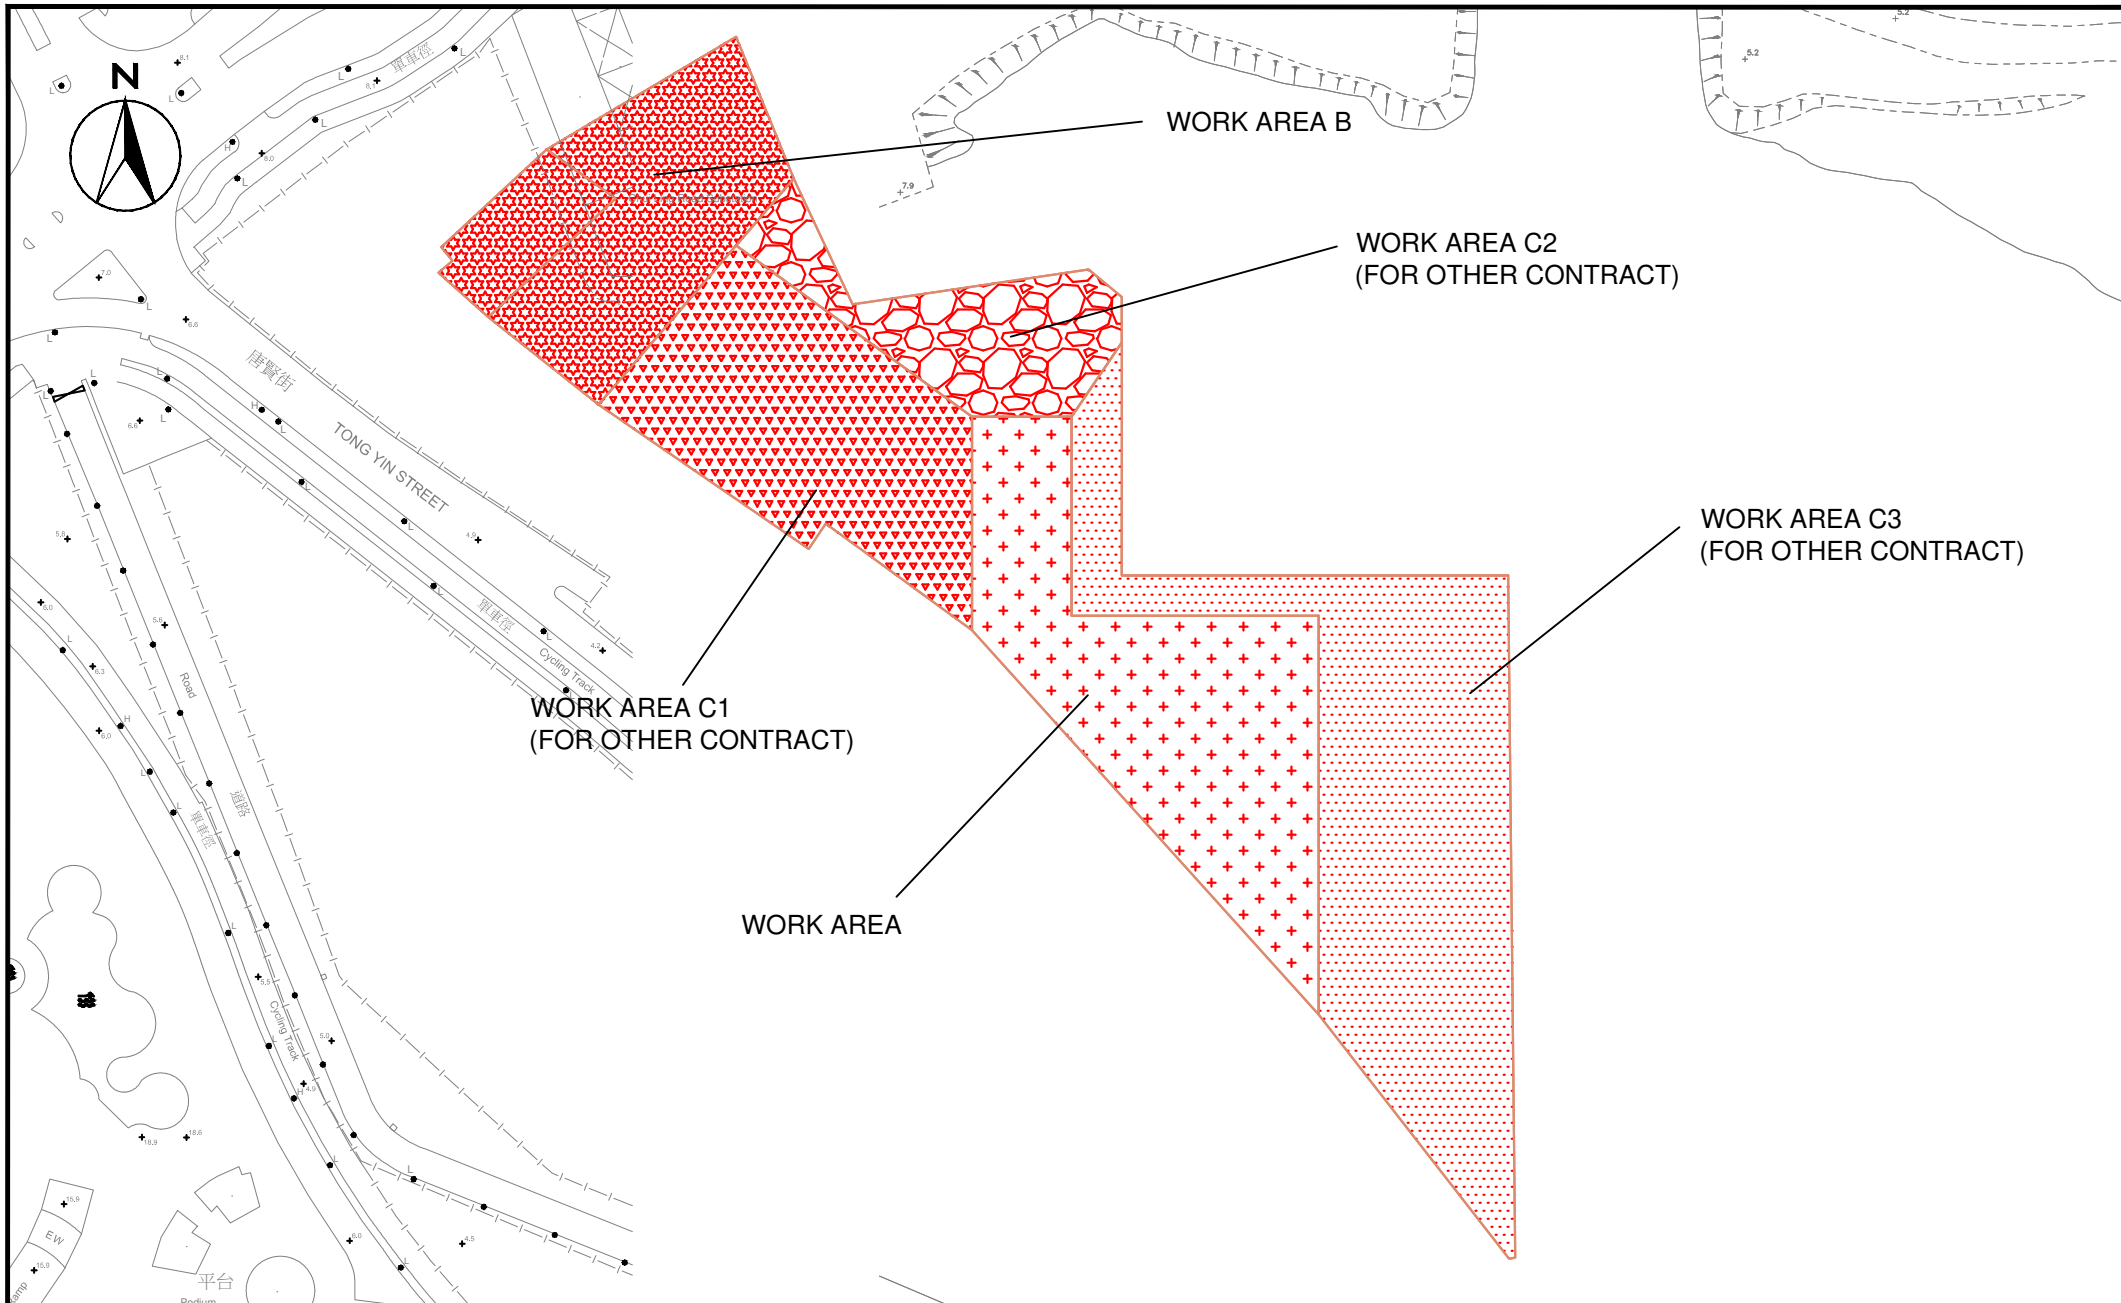

SCALE	1:1500 @ A4	DATE	JUN 2018	
CHECK	VC	DRAWN	AC	
JOB No.	MA16034	FIGURE NO.	1h	REV
				-

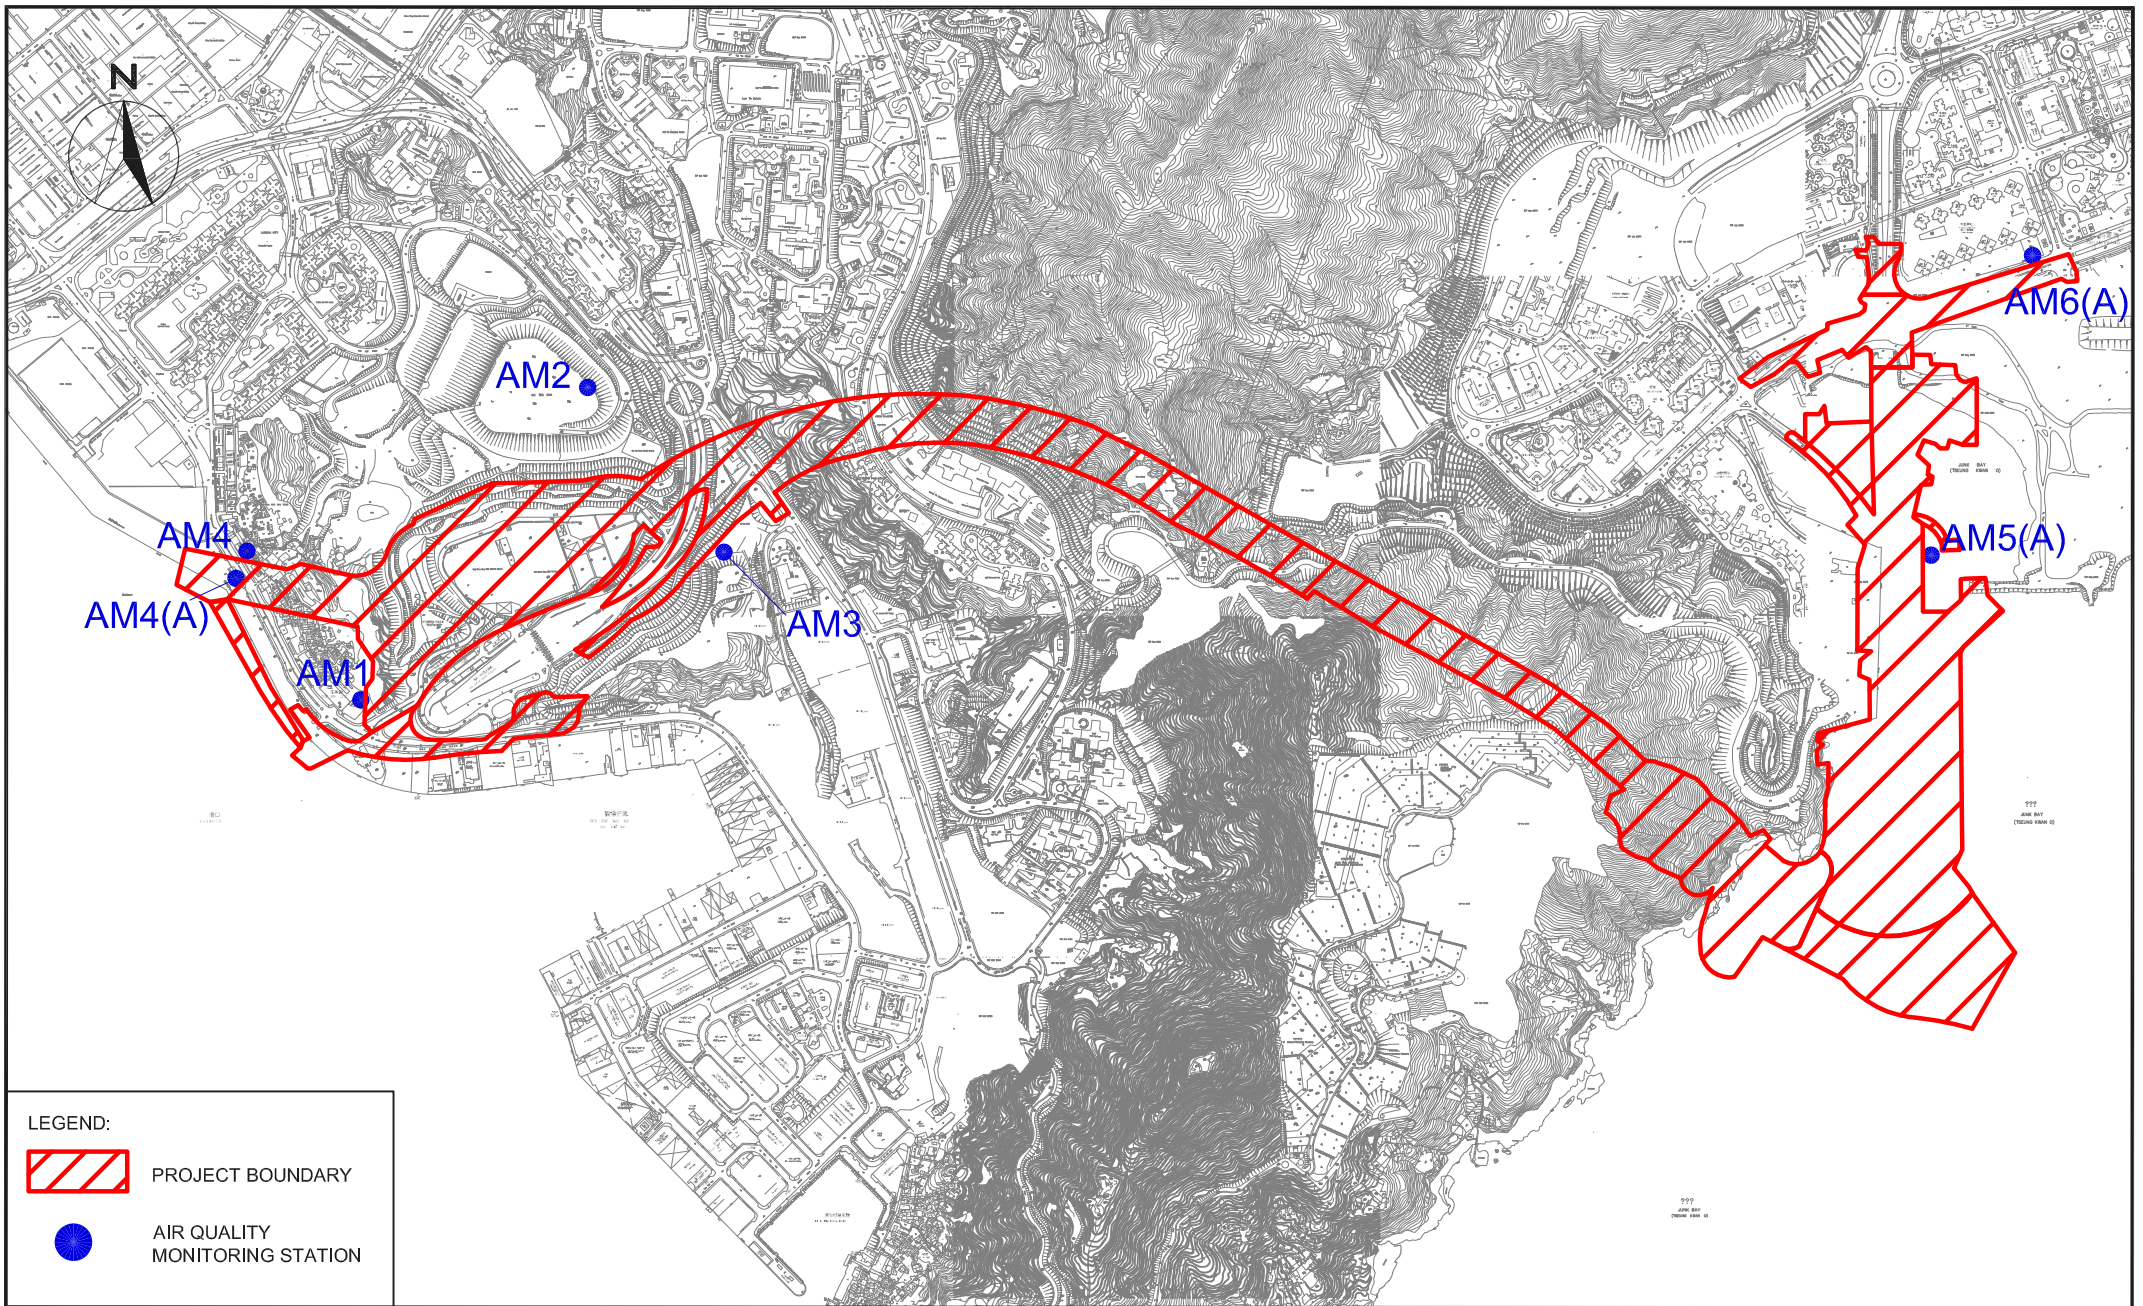

LEGEND:




PROJECT BOUNDARY





AIR QUALITY MONITORING STATION

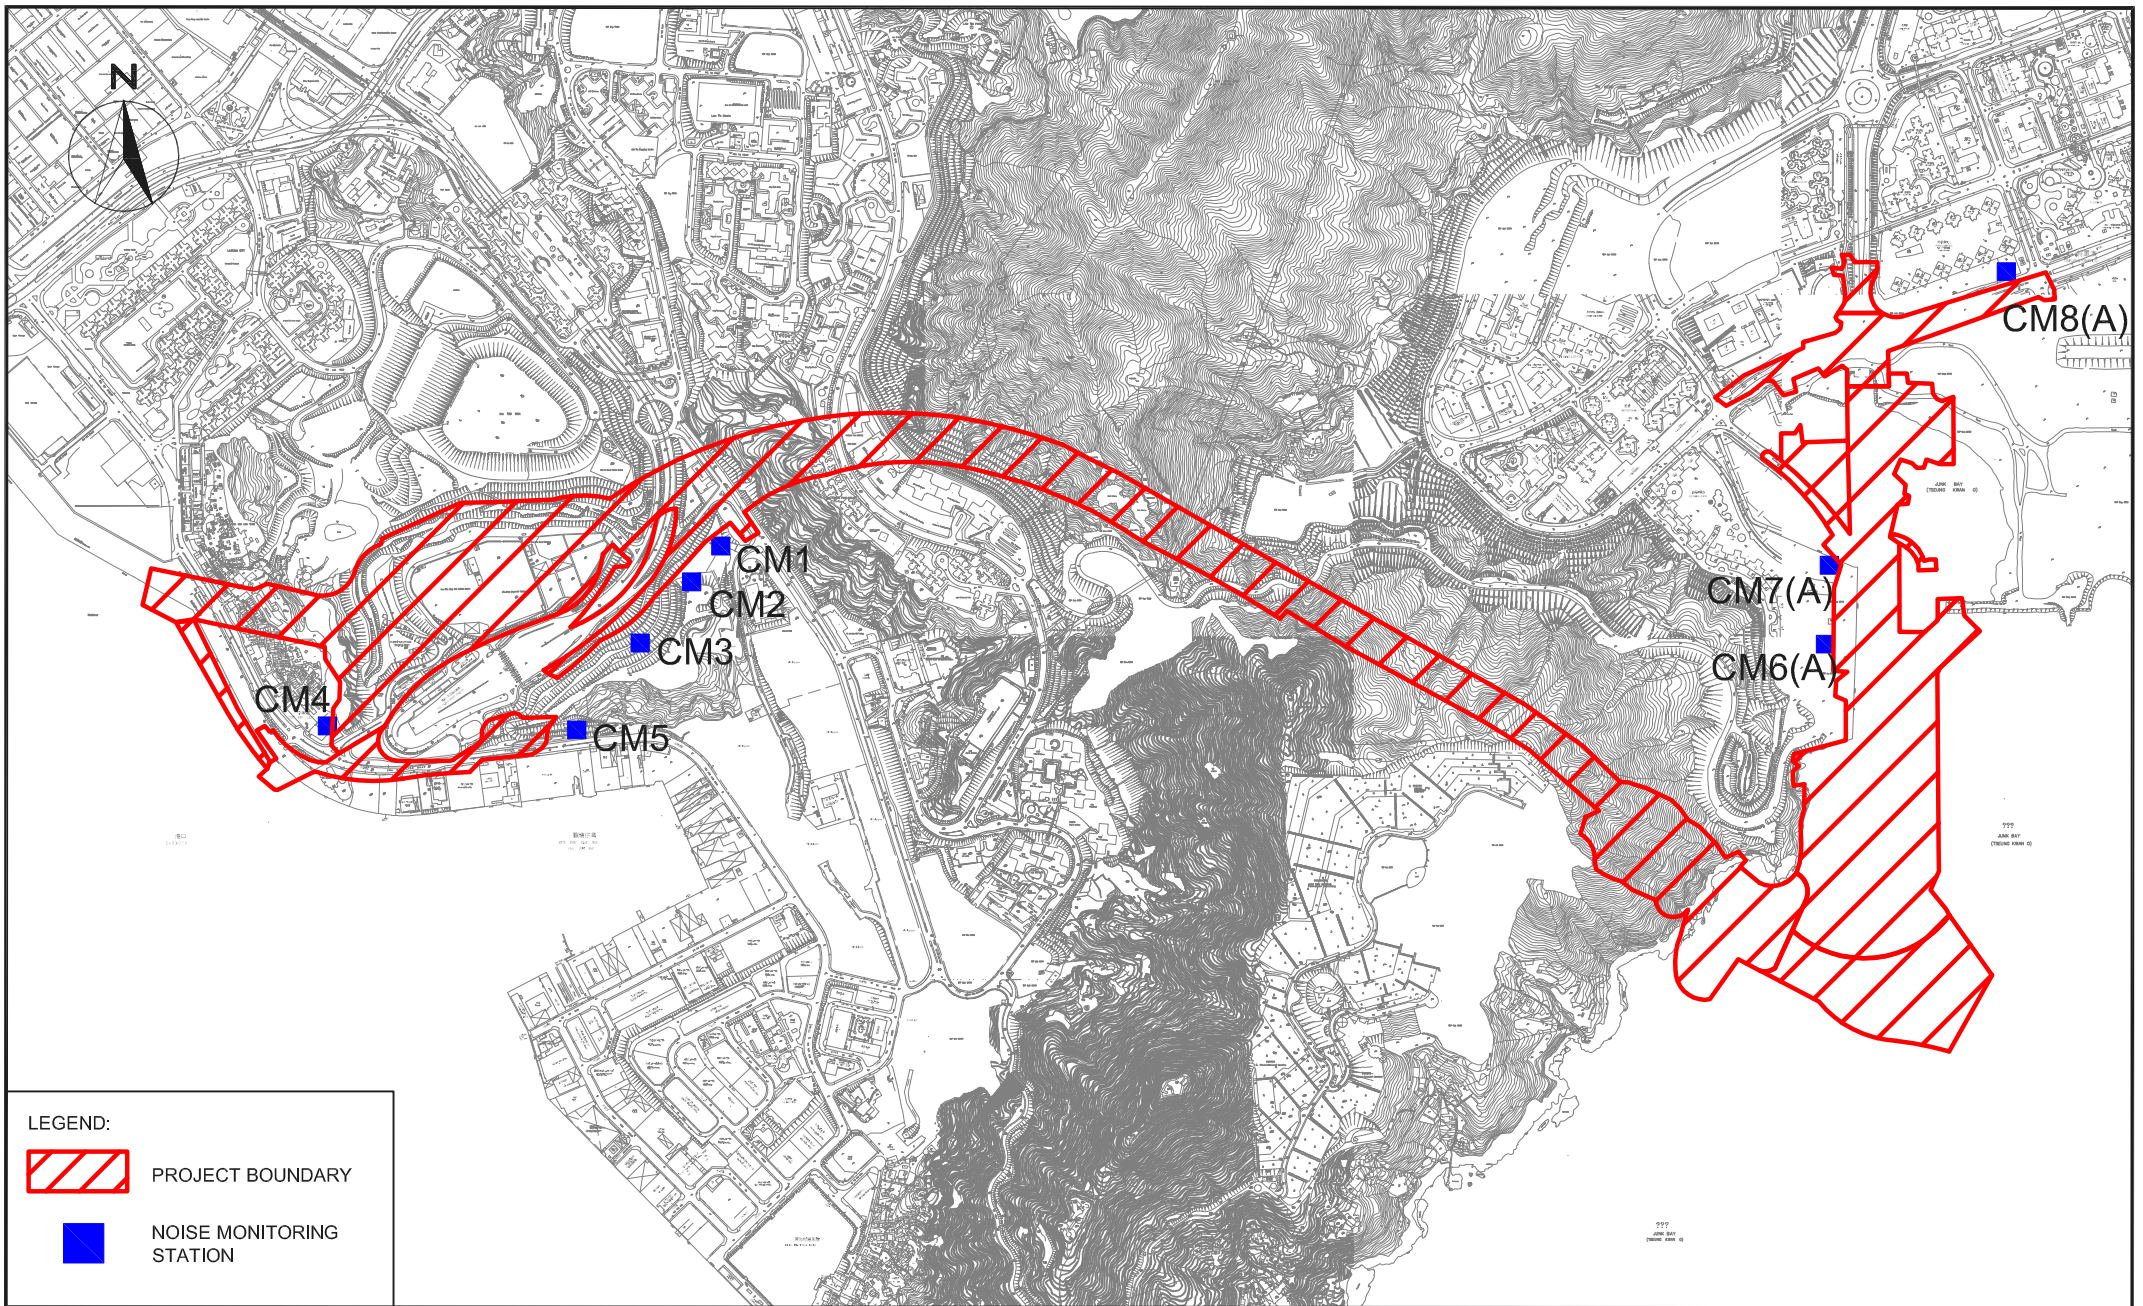
SCALE	1:15000 @ A4	DATE	JAN 2018	
CHECK	JF	DRAWN	JW	
JOB No.	MA16034	FIGURE NO.	2	REV -







LEGEND:

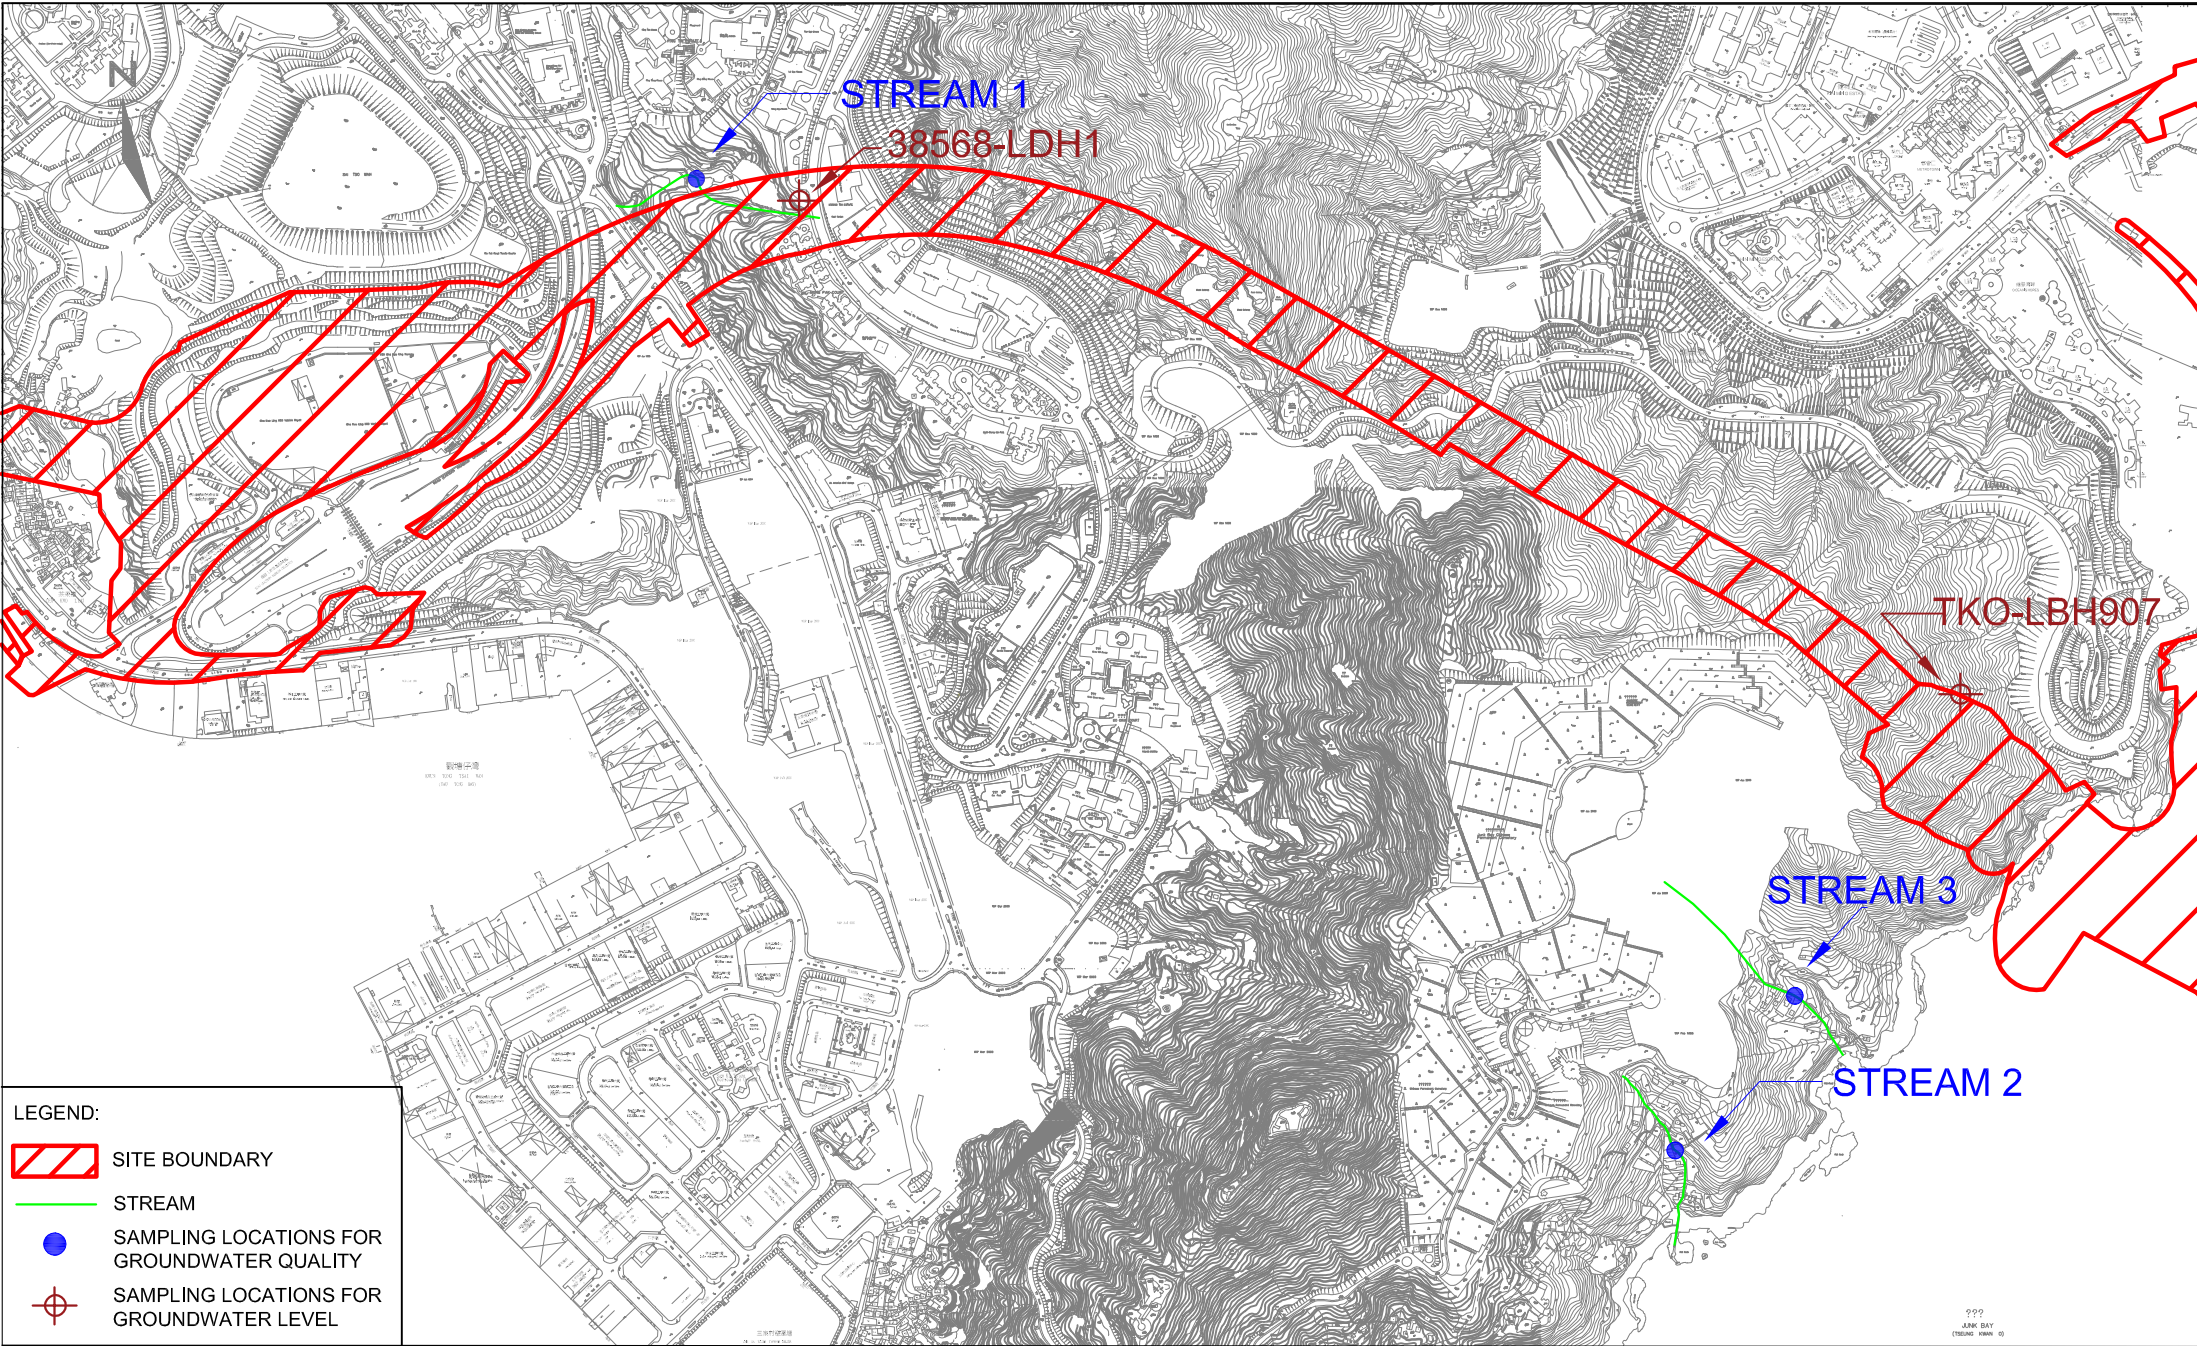-  PROJECT BOUNDARY
-  NOISE MONITORING STATION

SCALE	1:15000 @ A4	DATE	JAN 2018	
CHECK	JF	DRAWN	JW	
JOB No.	MA16034	FIGURE NO.	3	REV -




LEGEND:

-  SITE BOUNDARY
-  STREAM
-  SAMPLING LOCATIONS FOR GROUNDWATER QUALITY
-  SAMPLING LOCATIONS FOR GROUNDWATER LEVEL



Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel -
 Design and Construction
 Location of Streams for Groundwater Quality and Groundwater Level Monitoring

SCALE	1:10000 @ A4	DATE	APR 2017	
CHECK	JF	DRAWN	JW	
JOB No.	MA16034	FIGURE NO.	4	REV
				-

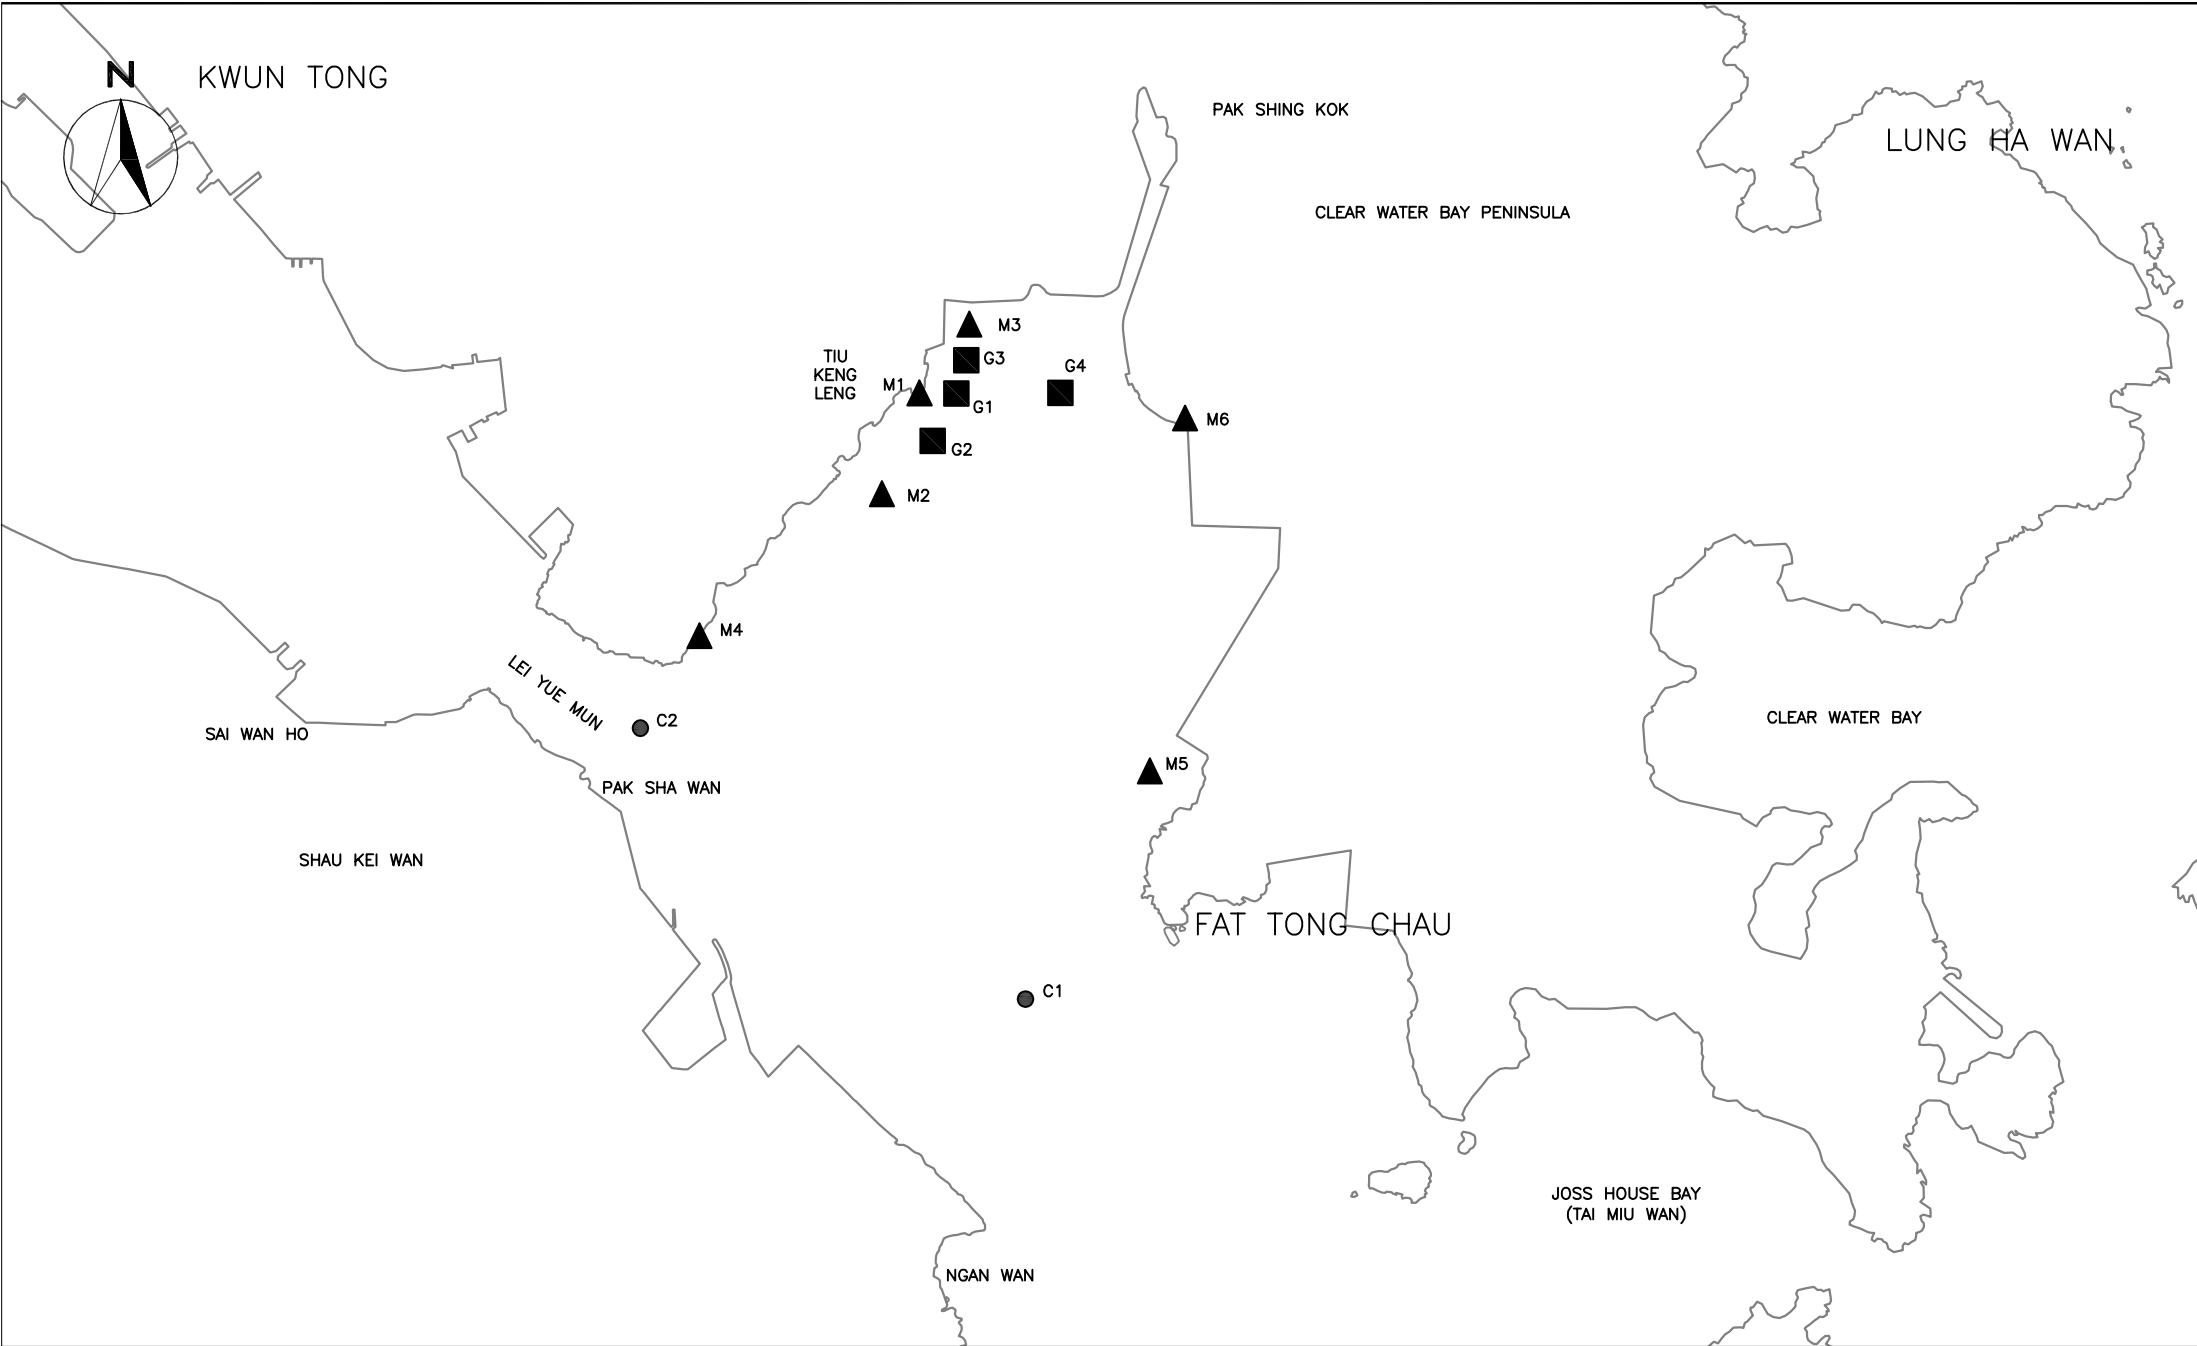

SCALE	N.T.S	DATE	AUG 2016	
CHECK	JF	DRAWN	JW	
PROJECT NO.	MA16034	FIGURE NO.	5	REV —




Title Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
 Locations of Landfill Gas Monitoring

Scale N.T.S
 Date Dec-16

Project No. MA16034
 Figure 6




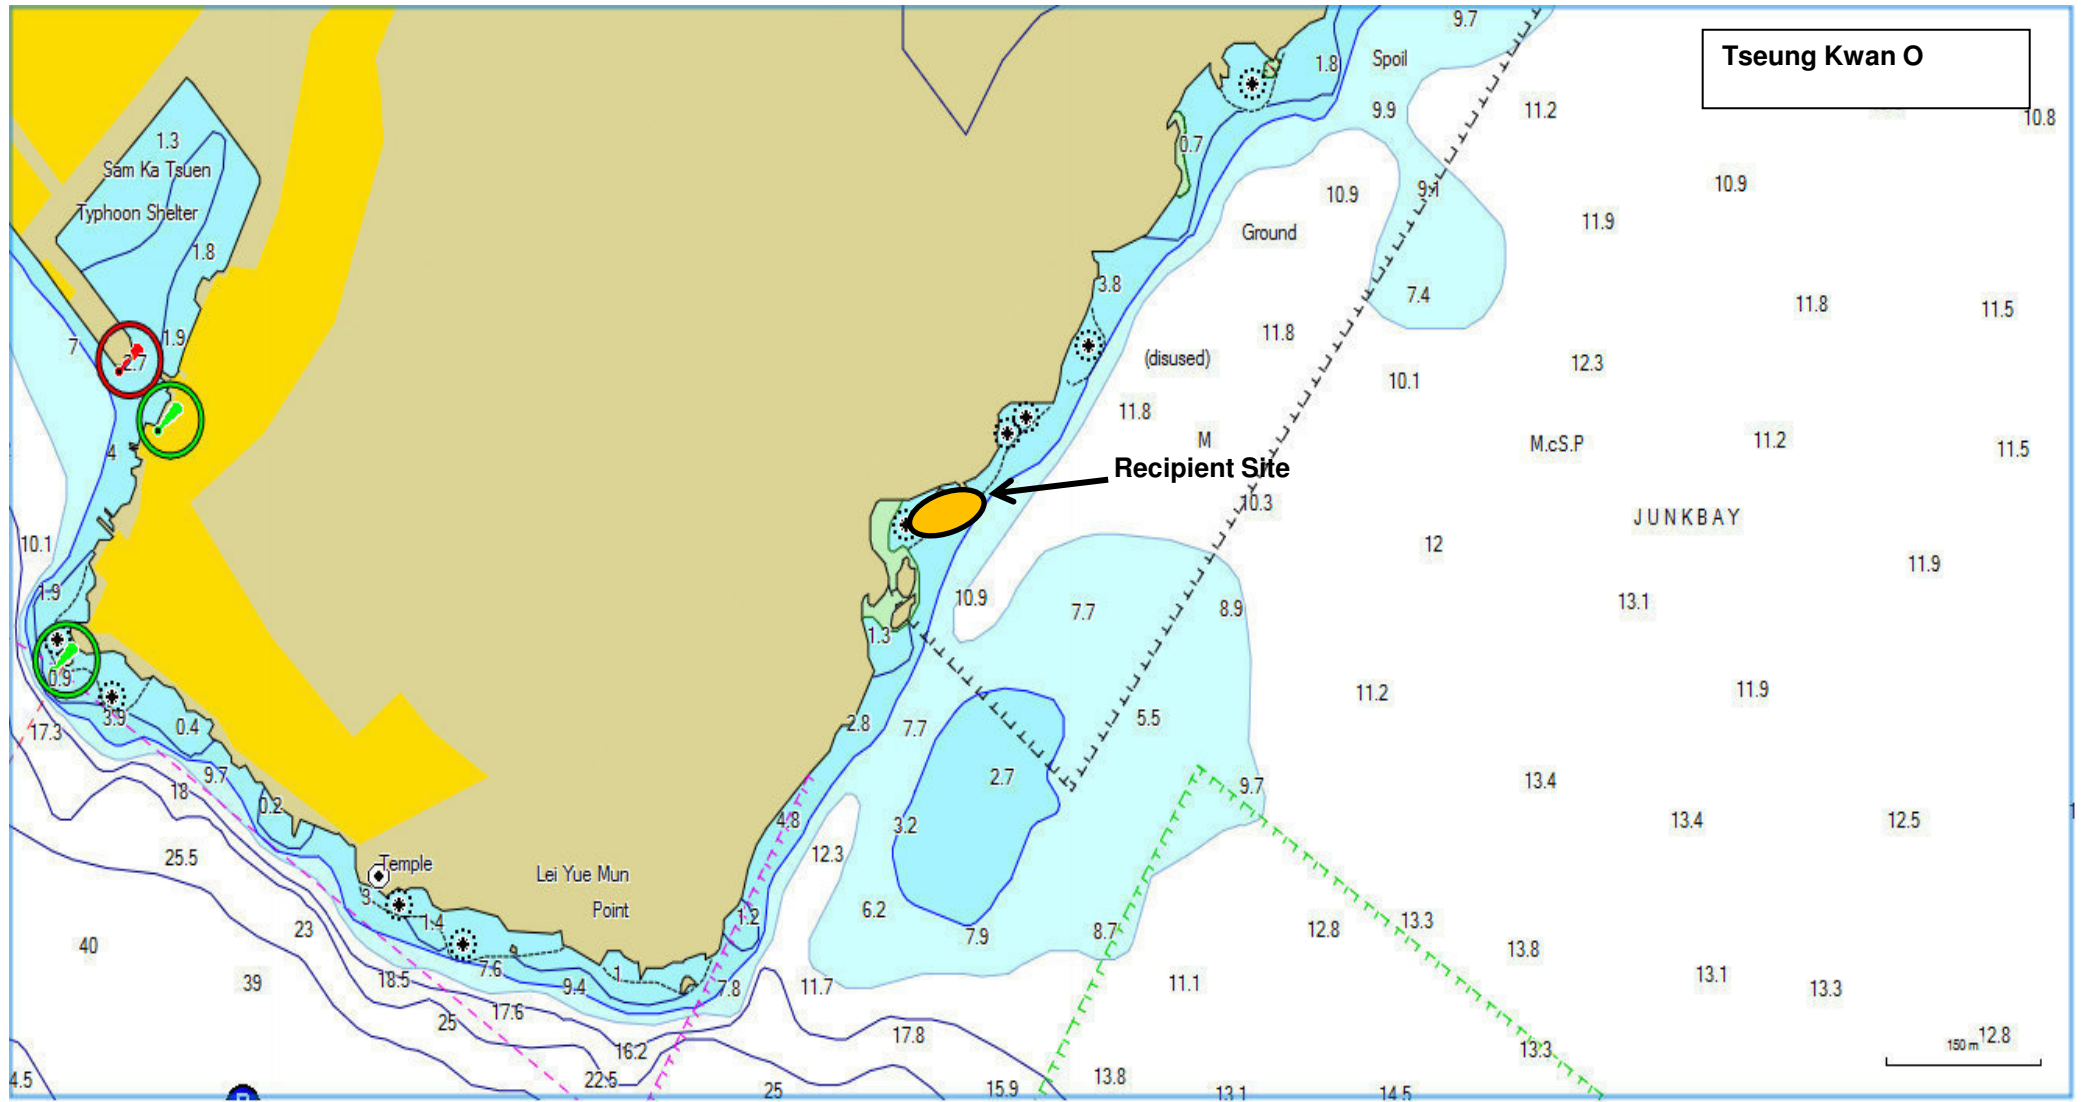


Title Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
 Location of Post-translocation Coral Monitoring

Scale N.T.S
 Date Mar-17

Project No. MA16034
 Figure 7





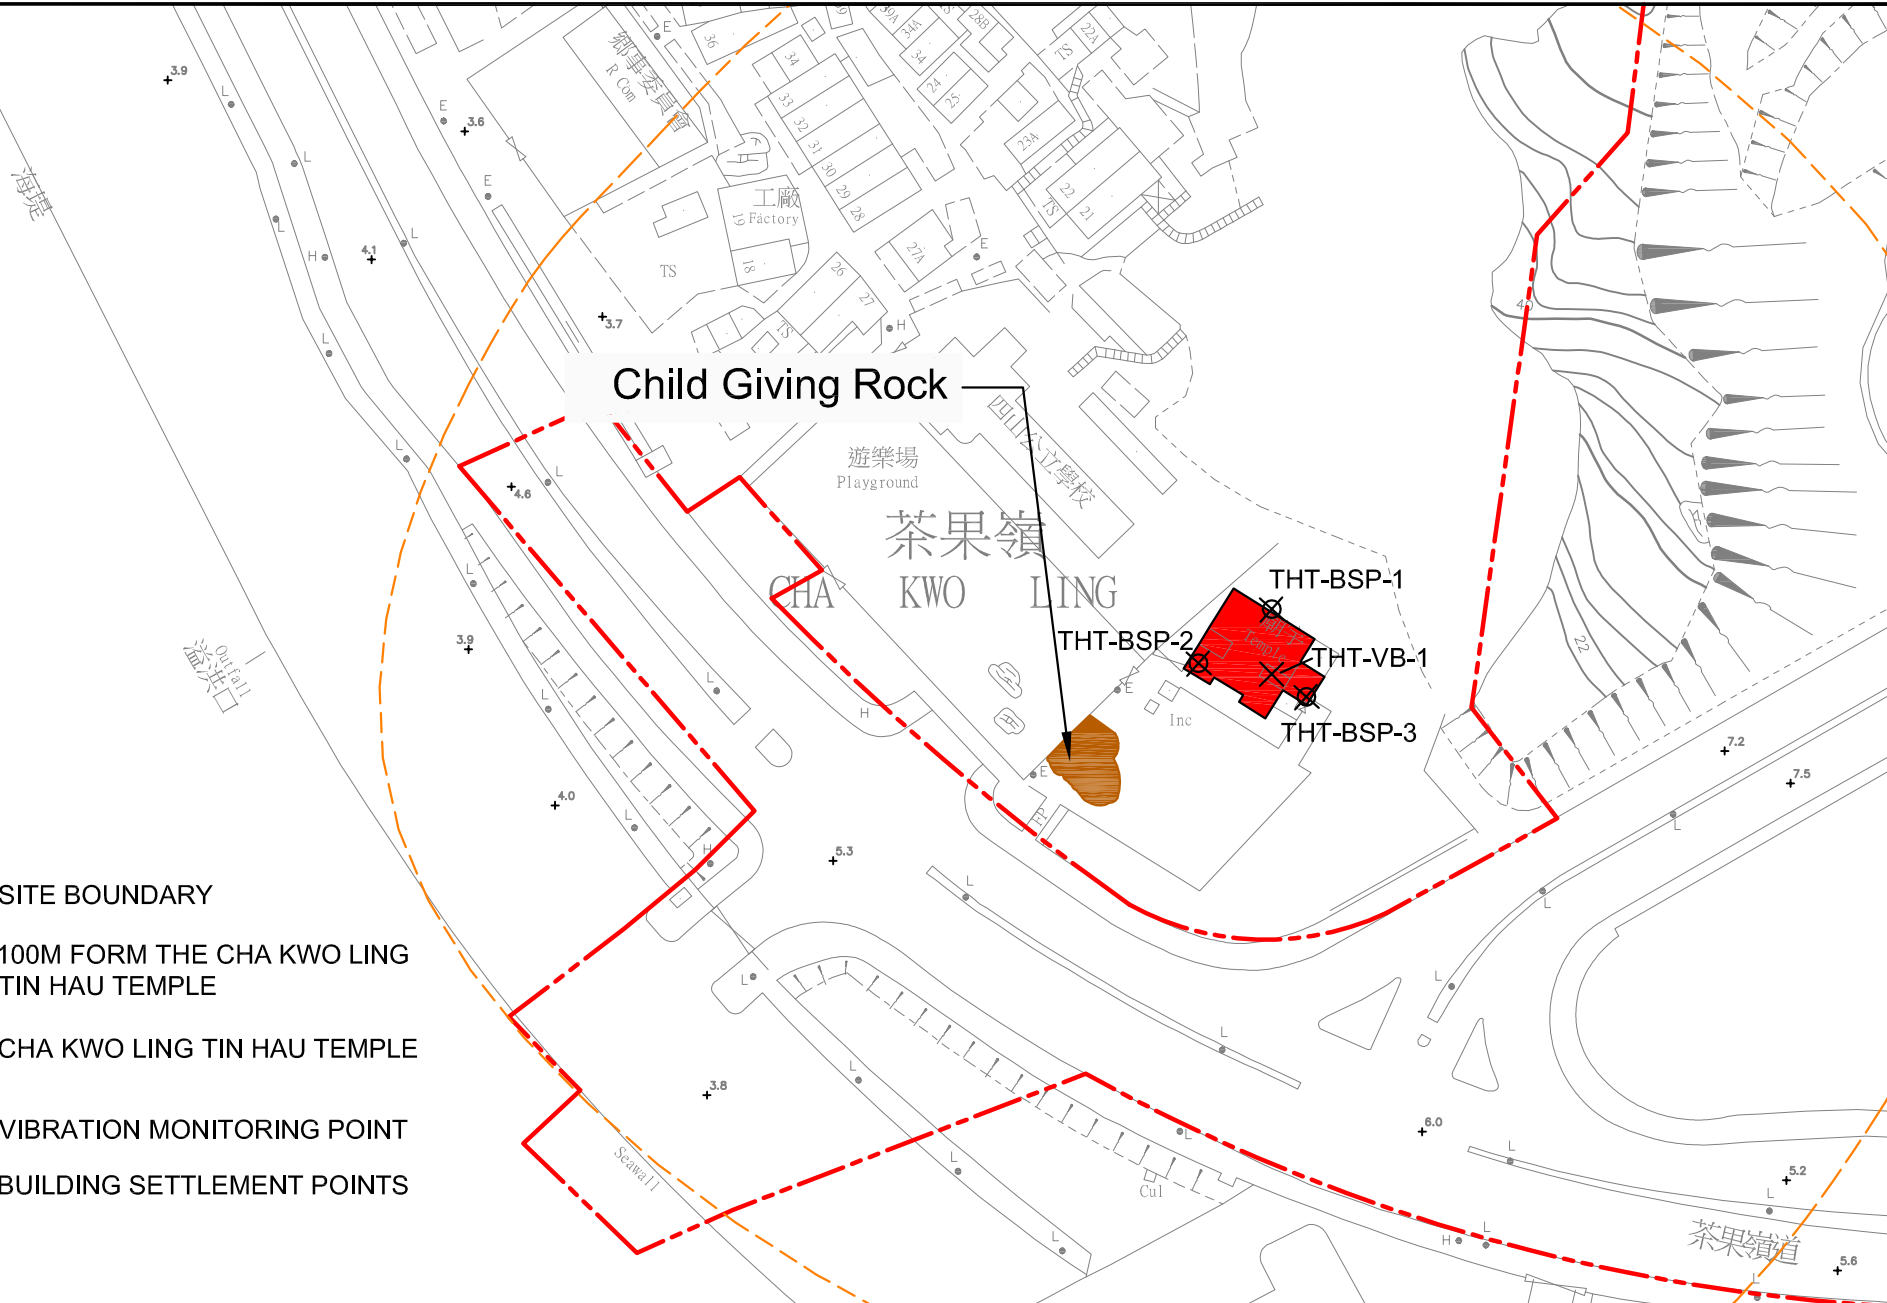

LEGEND

- - - SITE BOUNDARY
- - - 100M FORM THE CHA KWO LING TIN HAU TEMPLE
- CHA KWO LING TIN HAU TEMPLE
- ✕ VIBRATION MONITORING POINT
- ⊗ BUILDING SETTLEMENT POINTS


SCALE	N.T.S.	DATE	FEB 2018	
CHECK	JF	DRAWN	AC	
JOB No.	MA16034	FIGURE NO.	8	REV -

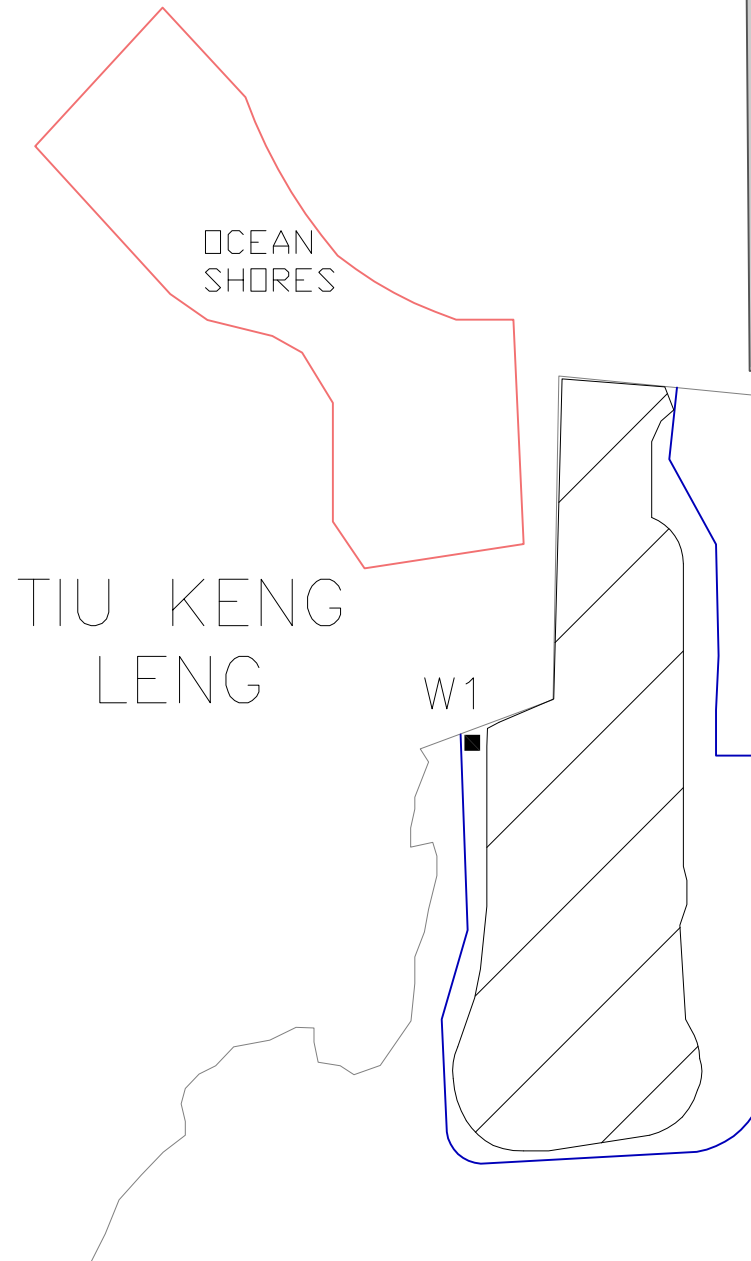

LEGEND



IMPACT STATIONS



LOCATION OF TEMPORARY MARINE EMBAYMENT BY STEEL COFFERDAM



RECLAMATION FOOTPRINT

CURRENT SHORELINE

**APPENDIX A
ACTION AND LIMIT LEVELS**

APPENDIX A – Action and Limit Levels

Air Quality

1-hr TSP

Monitoring Stations	Location	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AM1	Tin Hau Temple	275	500
AM2	Sai Tso Wan Recreation Ground	273	
AM3	Yau Lai Estate Bik Lai House	271	
AM4	Sitting-out Area at Cha Kwo Ling Village	278	
AM5(A)	Tseung Kwan O DSD Desilting Compound	273	
AM6(A)	Park Central, L1/F Open Space Area	285	

24-hr TSP

Monitoring Stations	Location	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AM1	Tin Hau Temple	173	260
AM2	Sai Tso Wan Recreation Ground	192	
AM3	Yau Lai Estate Bik Lai House	167	
AM4(A)	Cha Kwo Ling Public Cargo Working Area Administrative Office	210	
AM5(A)	Tseung Kwan O DSD Desilting Compound	175	
AM6(A)	Park Central, L1/F Open Space Area	165	

Noise

Time Period	Action Level	Limit Level
0700-1900 hrs on normal weekdays	When one documented complaint is received	75 dB(A) ⁽¹⁾
1900-2300 on all days and 0700-2300 on general holidays (including Sundays)		60/65/70 dB(A) ⁽²⁾⁽³⁾
2300-0700 on all days		45/50/55 dB(A) ⁽²⁾⁽³⁾

¹ 70 dB(A) for schools and 65 dB(A) for schools during examination period.

² Acceptable Noise Levels for Area Sensitivity Rating of A/B/C

³ If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.

Water Quality

Groundwater

Parameters	Action	Limit
DO in mg L ⁻¹	7.6	7.6
pH	6.0 – 8.9	6.0 – 9.0
BOD ₅ in mg L ⁻¹	2.0	2.0
TOC in mg L ⁻¹	Stream 1 and Stream 2: 9	Stream 1 and Stream 2: 9
	Stream 3: 6	Stream 3: 6
Total Nitrogen in mg L ⁻¹	2.0	2.1
Ammonia-N in mg L ⁻¹	0.15	0.20
Total Phosphate in mg L ⁻¹	0.05	0.05
SS in mg L ⁻¹	7.6	12.1
Turbidity in NTU	2.1	2.3

Notes:

1. For pH, non-compliance of the water quality limits occurs when monitoring result is out of the range of the limits.
2. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
3. For turbidity, SS, 5-day biochemical oxygen demand (BOD₅), Total organic carbon (TOC), Total Nitrogen, Ammonia-N and Total Phosphate, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
4. All the figures given in the table are used for reference only and the EPD may amend the figures whenever it is considered as necessary.

Groundwater Level Monitoring

Drill Hole No.	38568-LDH1	TKO-LBH907
Action Level (mPD)	+74.65	+17.59

Marine Water Quality

<u>Parameter (unit)</u>	<u>Depth</u>	<u>Action Level</u>	<u>Limit Level</u>
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2, 4 and 5)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
SS in mg/L (See Note 2, 4 and 5)	<u>Stations G1-G4</u>		
	Surface	<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day	<u>6.9mg/L</u> or 130% of upstream control station's SS at the same tide of the same day
	<u>Stations M1-M5</u>		
	Surface	<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day
	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day
	<u>Station M6</u>		
	Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.
5. Refer to Appendix I – Marine Water Quality Monitoring Results and Graphical Presentations for results of upstream control stations at each tide on each day.

Water Quality Monitoring in Temporary Marine Embayment

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 2)	Depth Average	<u>4.8 mg/L</u> ⁽⁴⁾	<u>4 mg/L</u> ⁽³⁾
	Bottom	<u>2.4 mg/L</u> ⁽⁴⁾	<u>2 mg/L</u> ⁽³⁾

Notes:

1. "depth-averaged" is calculated by taking the arithmetic means of reading of all sampling depths.
2. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
3. Current Water Quality Objectives (WQOs) for marine waters of Hong Kong
4. As an alert for adverse water quality impact, the Action Level is set as 120% of the Current WQOs for marine waters of Hong Kong.

Ecology

Post-translocation Coral Monitoring

Parameter	Action Level Definition	Limit Level Definition
Mortality	If during Impact Monitoring a 15% increase in the percentage of partial mortality on hard corals occurs at more than 20% of the tagged coral at any one Impact Monitoring Site that is not recorded at the Control Site, then the Action Level is exceeded.	If during the Impact Monitoring a 25% increase in the percentage of partial mortality occurs at more than 20% of the tagged coral at any one Impact Monitoring Site that is not recorded at the Control Site, then the Limit Level is exceeded.

Landfill Gas Monitoring

Parameter	Limit Level
Oxygen	<19%
	<18%
Methane	>10% LEL (i.e. > 0.5% by volume)
	>20% LEL (i.e. > 1% by volume)
Carbon Dioxide	>0.5%
	>1.5%

Alert, Alarm, Action Levels for Built Heritage Monitoring

Parameter	Alert Level	Alarm Level	Action Level
Vibration	ppv:4.5mm/s	ppv: 4.8mm/s	ppv: 5mm/s Maximum Allowable Vibration Amplitude: 0.1mm
Building Settlement Point	6mm	8mm	10mm
Building Tilting	1:2000	1:1500	1:1000

**APPENDIX B
COPIES OF CALIBRATION
CERTIFICATES**

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA16034/05/0010

Project No. AMI - Tin Hau Temple

Date: 2-Mar-18

Next Due Date: 1-May-18

Operator: MH

Equipment No.: A-01-05

Model No.: GS2310

Serial No.: 10599

Ambient Condition			
Temperature, Ta (K)	295.2	Pressure, Pa (mmHg)	763.0

Orifice Transfer Standard Information					
Serial No.	2896	Slope, mc	0.0585	Intercept, bc	-0.00045
Last Calibration Date:	13-Feb-18	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	13-Feb-19	$Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	ΔH (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	ΔW (HVS), in. of water	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	13.0	3.63	62.02	7.0	2.66
2	9.8	3.15	53.85	5.5	2.36
3	8.4	2.92	49.86	4.9	2.23
4	5.3	2.32	39.61	3.2	1.80
5	3.0	1.74	29.80	1.9	1.39

By Linear Regression of Y on X

Slope, mw = 0.0397

Intercept, bw = 0.2196

Correlation coefficient* = 0.9992

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 3.67

Remarks: _____

Conducted by: [Signature] Signature: _____

Date: 2/3/2018

Checked by: [Signature] Signature: _____

Date: 2/3/2018

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA16034/08/0010

Project No. AM2 - Sai Tso Wan Recreation Ground

Date: 2-Mar-18

Next Due Date: 1-May-18

Operator: MH

Equipment No.: A-01-08

Model No.: GS2310

Serial No.: 1287

Ambient Condition			
Temperature, Ta (K)	295.6	Pressure, Pa (mmHg)	762.9

Orifice Transfer Standard Information					
Serial No.	2896	Slope, mc	0.0585	Intercept, bc	-0.00045
Last Calibration Date:	13-Feb-18	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	13-Feb-19	$Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	ΔH (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X - axis	ΔW (HVS), in. of water	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	13.7	3.72	63.62	8.0	2.85
2	10.8	3.31	56.49	6.5	2.56
3	8.6	2.95	50.41	5.2	2.29
4	5.3	2.32	39.58	3.4	1.85
5	3.3	1.83	31.23	2.1	1.46

By Linear Regression of Y on X

Slope, mw = 0.0427

Intercept, bw = 0.1437

Correlation coefficient* = 0.9995

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; W = $(mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 3.87

Remarks: _____

Conducted by: Lee Man Ho Signature: _____

Date: 2-3-2018

Checked by: Wk Tang Signature: _____

Date: 2/3/2018

High-Volume TSP Sampler

5-POINT CALIBRATION DATA SHEET

CINOTECH

File No. MA16034/07/0010

Station AM6 - Park Central

Date: 26-Mar-18

Next Due Date: 25-May-18

Operator: MH

Equipment No.: A-01-07

Model No.: GS2310

Serial No.: 10592

Ambient Condition			
Temperature, Ta (K)	297.2	Pressure, Pa (mmHg)	765.4

Orifice Transfer Standard Information					
Serial No.	2896	Slope, mc	0.0585	Intercept, bc	-0.00045
Last Calibration Date:	13-Feb-18	$mc \times Qstd + bc = [\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	13-Feb-19	$Qstd = \{[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Calibration Point	Orifice			HVS	
	ΔH (orifice), in. of water	$[\Delta H \times (Pa/760) \times (298/Ta)]^{1/2}$	Qstd (CFM) X-axis	ΔW (HVS), in. of water	$[\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$ Y-axis
1	11.6	3.42	58.48	7.7	2.79
2	9.7	3.13	53.48	6.4	2.54
3	7.4	2.73	46.71	4.9	2.22
4	5.3	2.31	39.53	3.6	1.91
5	3.5	1.88	32.13	2.3	1.52

By Linear Regression of Y on X

Slope, mw = 0.0475

Intercept, bw = 0.0101

Correlation coefficient* = 0.9997

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 43 CFM

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = [\Delta W \times (Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; $W = (mw \times Qstd + bw)^2 \times (760 / Pa) \times (Ta / 298) =$ 4.17

Remarks: _____

Conducted by: LEE MAN HEI Signature: _____

Date: 26-3-2018

Checked by: W.K. Tang Signature: _____

Date: 26-3-2018



RECALIBRATION
DUE DATE:
February 13, 2019

Certificate of Calibration

Calibration Certification Information			
Cal. Date: February 13, 2018	Rootsmeter S/N: 438320	Ta: 293	°K
Operator: Jim Tisch		Pa: 763.3	mm Hg
Calibration Model #: TE-5025A	Calibrator S/N: 2896		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4670	3.2	2.00
2	3	4	1	1.0380	6.4	4.00
3	5	6	1	0.9220	8.0	5.00
4	7	8	1	0.8840	8.8	5.50
5	9	10	1	0.7250	12.8	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
1.0172	0.6934	1.4293	0.9958	0.6788	0.8762
1.0129	0.9758	2.0213	0.9916	0.9553	1.2392
1.0107	1.0962	2.2599	0.9895	1.0732	1.3854
1.0097	1.1422	2.3702	0.9885	1.1182	1.4530
1.0043	1.3853	2.8586	0.9832	1.3562	1.7524
QSTD	m=	2.06726	QA	m=	1.29448
	b=	-0.00045		b=	-0.00028
	r=	0.99992		r=	0.99992

Calculations	
$Vstd = \Delta Vol \left(\frac{Pa - \Delta P}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)$	$Va = \Delta Vol \left(\frac{Pa - \Delta P}{Pa} \right)$
$Qstd = Vstd / \Delta Time$	$Qa = Va / \Delta Time$
For subsequent flow rate calculations:	
$Qstd = 1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	$Qa = 1/m \left(\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	C/W/180127
Date of Issue:	2018-01-28
Date Received:	2018-01-27
Date Tested:	2018-01-27
Date Completed:	2018-01-28
Next Due Date:	2018-07-27

ATTN: Mr. W.K. Tang

Page: 1 of 2

Certificate of Calibration

Item for calibration:

Description : Weather Stations, Vantage Pro2
Manufacturer : Davis Instruments
Model No. : 6152CUK
Serial No. : AK130520007

Test conditions:

Room Temperature : 21 degree Celsius
Relative Humidity : 56 %

Test Specifications:


1. Performance check of anemometer
2. Performance check of wind direction sensor

Methodology:

In-house method with reference anemometer (RS232 Integral Vane Digital Anemometer)

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE

Laboratory Manager

TEST REPORT

Test Report No.:	C/W/180127
Date of Issue:	2018-01-28
Date Received:	2018-01-27
Date Tested:	2018-01-27
Date Completed:	2018-01-28
Next Due Date:	2018-07-27
Page:	2 of 2

Results:

1. Performance check of anemometer

Air Velocity, m/s		Difference D (m/s)
Instrument Reading (V1)	Reference Value (V1)	D = V1 - V2
2.00	2.00	0.00

2. Performance check of wind direction sensor

Wind Direction (°)		Difference D (°)
Instrument Reading (W1)	Reference Value (W2)	D = W1 - W2
0	0	0
45.3	45	0.3
90.1	90	0.1
135	135	0
180.1	180	0.1
225.2	225	0.2
270.2	270	0.2
315	315	0
360	360	0

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Test Report No.:	28394
Date of Issue:	2018-02-25
Date Received:	2018-02-24
Date Tested:	2018-02-24 to 2018-02-25
Date Completed:	2018-02-25
Next Due Date:	2018-05-24

ATTN: Miss Mei Ling Tang

Page: 1 of 2

Certificate of Calibration

Item for calibration:

YSI EXO1 Multiparameter Sondes	Equipment No.: SW-08-03	
Manufacturer:	YSI Incorporated, a Xylem brand	
Description:	Model No.	Serial No.
- EXO Optical DO Sensor, Ti	599100-01	16H102982
- EXO conductivity/Temperature Sensor, Ti	599870	16G102304
- EXO Turbidity Sensor, Ti	599101-01	16H102460
- EXO pH Sensor Assembly, Guarded, Ti	599701	16J100413

Test conditions:

Room Temperature : 17-22 degree Celsius
Relative Humidity : 40-70%

Test Specifications:

Performance checking for Conductivity, Temperature, pH, Dissolved oxygen (D.O.) and Turbidity

Methodology:

According to manufacturer instruction manual, APHA 20e 4500-O C

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

Test Report No.:	28394
Date of Issue:	2018-02-25
Date Received:	2018-02-24
Date Tested:	2018-02-24 to 2018-02-25
Date Completed:	2018-02-25
Next Due Date:	2018-05-24

Page: 2 of 2

Certificate of Calibration

Results:

Conductivity performance checking

	Instrument Readings ($\mu\text{S}/\text{cm}$)	Acceptance Criteria	Comment
KCl stock solution (12890 $\mu\text{S}/\text{cm}$)	13000	12246-13534	Pass

Temperature performance checking

Reference thermometer- E431 Readings ($^{\circ}\text{C}$)	Instrument Readings ($^{\circ}\text{C}$)	Correction ($^{\circ}\text{C}$)	Comment
20.7	20.704	-0.004	N/A

pH performance checking

	Instrument Readings (pH unit)	Acceptance Criteria	Comment
pH QC buffer 4.00	4.01	4.00 ± 0.10	Pass
pH QC buffer 6.86	6.89	6.86 ± 0.10	Pass
pH QC buffer 9.18	9.18	9.18 ± 0.10	Pass

D.O. performance checking

	Instrument Readings (mg/L)	Acceptance Criteria	Comment
Zero DO solution	0.05	$<0.1\text{mg}/\text{L}$	Pass

Winkler Titration value (mg/L)	Instrument Readings (mg/L)	Acceptance Criteria	Comment
8.00	8.05	Difference between Titration value and instrument reading $<0.2\text{mg}/\text{L}$	Pass

Turbidity performance checking

Turbidity stock solution	Instrument Readings (NTU)	Acceptance Criteria	Comment
10 NTU	10.02	9.0-11.0	Pass
50 NTU	50.07	45.0-55.0	Pass
100 NTU	100.5	90.0-110.0	Pass

Depth performance checking

Water Depth	Instrument Readings (NTU)	Acceptance Criteria	Comment
0.5 meter	0.50	0.45-0.55	Pass

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Test Report No.:	28394A
Date of Issue:	2018-02-25
Date Received:	2018-02-24
Date Tested:	2018-02-24 to 2018-02-25
Date Completed:	2018-02-25
Next Due Date:	2018-05-24

ATTN: Miss Mei Ling Tang

Page: 1 of 2

Certificate of Calibration

Item for calibration:

YSI EXO1 Multiparameter Sondes	Equipment No.:	SW-08-06
Manufacturer:	YSI Incorporated, a Xylem brand	
Description:	Model No.	Serial No.
- EXO Optical DO Sensor, Ti	599100-01	16H102985
- EXO conductivity/Temperature Sensor, Ti	599870	16G102307
- EXO Turbidity Sensor, Ti	599101-01	16H102463
- EXO pH Sensor Assembly, Guarded, Ti	599701	16H102985

Test conditions:

Room Temperature : 17-22 degree Celsius
Relative Humidity : 40-70%

Test Specifications:

Performance checking for Conductivity, Temperature, pH, Dissolved oxygen (D.O.)
and Turbidity

Methodology:

According to manufacturer instruction manual, APHA 20e 4500-O C

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

Test Report No.:	28394A
Date of Issue:	2018-02-25
Date Received:	2018-02-24
Date Tested:	2018-02-24 to 2018-02-25
Date Completed:	2018-02-25
Next Due Date:	2018-05-24

Page: 2 of 2

Certificate of Calibration

Results:

Conductivity performance checking

	Instrument Readings ($\mu\text{S}/\text{cm}$)	Acceptance Criteria	Comment
KCl stock solution (12890 $\mu\text{S}/\text{cm}$)	13000	12246-13534	Pass

Temperature performance checking

Reference thermometer- E431 Readings ($^{\circ}\text{C}$)	Instrument Readings ($^{\circ}\text{C}$)	Correction ($^{\circ}\text{C}$)	Comment
20.7	20.704	-0.004	N/A

pH performance checking

	Instrument Readings (pH unit)	Acceptance Criteria	Comment
pH QC buffer 4.00	4.00	4.00 \pm 0.10	Pass
pH QC buffer 6.86	6.86	6.86 \pm 0.10	Pass
pH QC buffer 9.18	9.20	9.18 \pm 0.10	Pass

D.O. performance checking

	Instrument Readings (mg/L)	Acceptance Criteria	Comment
Zero DO solution	0.05	<0.1mg/L	Pass

Winkler Titration value (mg/L)	Instrument Readings (mg/L)	Acceptance Criteria	Comment
8.00	8.03	Difference between Titration value and instrument reading <0.2mg/L	Pass

Turbidity performance checking

Turbidity stock solution	Instrument Readings (NTU)	Acceptance Criteria	Comment
10 NTU	10.03	9.0-11.0	Pass
50 NTU	50.05	45.0-55.0	Pass
100 NTU	100.4	90.0-110.0	Pass

Depth performance checking

Water Depth	Instrument Readings (NTU)	Acceptance Criteria	Comment
0.5 meter	0.50	0.45-0.55	Pass

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Test Report No.:	28394B
Date of Issue:	2018-02-25
Date Received:	2018-02-24
Date Tested:	2018-02-24 to 2018-02-25
Date Completed:	2018-02-25
Next Due Date:	2018-05-24

ATTN: Miss Mei Ling Tang

Page: 1 of 2

Certificate of Calibration

Item for calibration:

YSI EXO1 Multiparameter Sondes	Equipment No.: SW-08-09	
Manufacturer:	YSI Incorporated, a Xylem brand	
Description:	Model No.	Serial No.
- EXO Optical DO Sensor, Ti	599100-01	16H102988
- EXO conductivity/Temperature Sensor, Ti	599870	16G102310
- EXO Turbidity Sensor, Ti	599101-01	16H102467
- EXO pH Sensor Assembly, Guarded, Ti	599701	16J100419

Test conditions:

Room Temperature : 17-22 degree Celsius
Relative Humidity : 40-70%

Test Specifications:

Performance checking for Conductivity, Temperature, pH, Dissolved oxygen (D.O.) and Turbidity

Methodology:

According to manufacturer instruction manual, APHA 20e 4500-O C

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

Test Report No.:	28394B
Date of Issue:	2018-02-25
Date Received:	2018-02-24
Date Tested:	2018-02-24 to 2018-02-25
Date Completed:	2018-02-25
Next Due Date:	2018-05-24

Page: 2 of 2

Certificate of Calibration

Results:

Conductivity performance checking

	Instrument Readings ($\mu\text{S}/\text{cm}$)	Acceptance Criteria	Comment
KCl stock solution (12890 $\mu\text{S}/\text{cm}$)	13000	12246-13534	Pass

Temperature performance checking

Reference thermometer- E431 Readings ($^{\circ}\text{C}$)	Instrument Readings ($^{\circ}\text{C}$)	Correction ($^{\circ}\text{C}$)	Comment
20.7	20.704	-0.004	N/A

pH performance checking

	Instrument Readings (pH unit)	Acceptance Criteria	Comment
pH QC buffer 4.00	4.07	4.00 ± 0.10	Pass
pH QC buffer 6.86	6.89	6.86 ± 0.10	Pass
pH QC buffer 9.18	9.22	9.18 ± 0.10	Pass

D.O. performance checking

	Instrument Readings (mg/L)	Acceptance Criteria	Comment
Zero DO solution	0.05	$<0.1\text{mg}/\text{L}$	Pass

Winkler Titration value (mg/L)	Instrument Readings (mg/L)	Acceptance Criteria	Comment
8.00	8.01	Difference between Titration value and instrument reading $<0.2\text{mg}/\text{L}$	Pass

Turbidity performance checking

Turbidity stock solution	Instrument Readings (NTU)	Acceptance Criteria	Comment
10 NTU	10.23	9.0-11.0	Pass
50 NTU	50.18	45.0-55.0	Pass
100 NTU	100.4	90.0-110.0	Pass

Depth performance checking

Water Depth	Instrument Readings (NTU)	Acceptance Criteria	Comment
0.5 meter	0.50	0.45-0.55	Pass

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Test Report No.:	28394C
Date of Issue:	2018-02-25
Date Received:	2018-02-24
Date Tested:	2018-02-24 to 2018-02-25
Date Completed:	2018-02-25
Next Due Date:	2018-05-24

ATTN: Miss Mei Ling Tang

Page: 1 of 2

Certificate of Calibration

Item for calibration:

YSI EXO1 Multiparameter Sondes	Equipment No.:	SW-08-20
Manufacturer:	YSI Incorporated, a Xylem brand	
Description:	Model No.	Serial No.
- EXO Optical DO Sensor, Ti	599100-01	16J100944
- EXO conductivity/Temperature Sensor, Ti	599870	16H100178
- EXO Turbidity Sensor, Ti	599101-01	16J101097
- EXO pH Sensor Assembly, Guarded, Ti	599701	16J100706

Test conditions:

Room Temperature : 17-22 degree Celsius
Relative Humidity : 40-70%

Test Specifications:

Performance checking for Conductivity, Temperature, pH, Dissolved oxygen (D.O.) and Turbidity

Methodology:

According to manufacturer instruction manual, APHA 20e 4500-O C

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

Test Report No.:	28394C
Date of Issue:	2018-02-25
Date Received:	2018-02-24
Date Tested:	2018-02-24 to 2018-02-25
Date Completed:	2018-02-25
Next Due Date:	2018-05-24

Page: 2 of 2

Certificate of Calibration

Results:

Conductivity performance checking

	Instrument Readings ($\mu\text{S/cm}$)	Acceptance Criteria	Comment
KCl stock solution (12890 $\mu\text{S/cm}$)	13000	12246-13534	Pass

Temperature performance checking

	Instrument Readings ($^{\circ}\text{C}$)	Correction ($^{\circ}\text{C}$)	Comment
Reference thermometer- E431 Readings ($^{\circ}\text{C}$)	20.002	-0.002	N/A

pH performance checking

	Instrument Readings (pH unit)	Acceptance Criteria	Comment
pH QC buffer 4.00	4.00	4.00 ± 0.10	Pass
pH QC buffer 6.86	6.88	6.86 ± 0.10	Pass
pH QC buffer 9.18	9.20	9.18 ± 0.10	Pass

D.O. performance checking

	Instrument Readings (mg/L)	Acceptance Criteria	Comment
Zero DO solution	0.05	$<0.1\text{mg/L}$	Pass

	Instrument Readings (mg/L)	Acceptance Criteria	Comment
Winkler Titration value (mg/L)	8.08	Difference between Titration value and instrument reading $<0.2\text{mg/L}$	Pass

Turbidity performance checking

	Instrument Readings (NTU)	Acceptance Criteria	Comment
Turbidity stock solution			
10 NTU	10.22	9.0-11.0	Pass
50 NTU	50.50	45.0-55.0	Pass
100 NTU	100.8	90.0-110.0	Pass

Depth performance checking

	Instrument Readings (NTU)	Acceptance Criteria	Comment
Water Depth			
0.5 meter	0.50	0.45-0.55	Pass

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	28393
Date of Issue:	2018-22-26
Date Received:	2018-02-23
Date Tested:	2018-02-23
Date Completed:	2018-02-26
Next Due Date:	2018-04-25

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description	: Handheld Particle Counter
Manufacturer	: Hal Technology
Model No.	: Hal-HPC300
Serial No.	: 3020408
Flow rate	: 0.1 cfm
Zero Count Test	: 0 count per 5 minutes
Equipment No.	: A-26-01

Test Conditions:

Room Temperature	: 17-22 degree Celsius
Relative Humidity	: 40-70%

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

Correlation Factor (CF)	1.104
-------------------------	-------

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	28393B
Date of Issue:	2018-22-26
Date Received:	2018-02-23
Date Tested:	2018-02-23
Date Completed:	2018-02-26
Next Due Date:	2018-04-25

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description : Handheld Particle Counter
 Manufacturer : Hal Technology
 Model No. : Hal-HPC300
 Serial No. : 3020410
 Flow rate : 0.1 cfm
 Zero Count Test : 0 count per 5 minutes
 Equipment No. : A-26-03

Test Conditions:

Room Temperature : 17-22 degree Celsius
 Relative Humidity : 40-70%

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

Correlation Factor (CF)	1.164
-------------------------	-------

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE

Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	28392
Date of Issue:	2018-02-20
Date Received:	2018-02-15
Date Tested:	2018-02-15
Date Completed:	2018-02-20
Next Due Date:	2018-04-19

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description	: Handheld Particle Counter
Manufacturer	: Hal Technology
Model No.	: Hal-HPC301
Serial No.	: 3011701019
Flow rate	: 0.1 cfm
Zero Count Test	: 0 count per 5 minutes
Equipment No.	: A-27-01

Test Conditions:

Room Temperature	: 17-22 degree Celsius
Relative Humidity	: 40-70%

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

Correlation Factor (CF)	1.223
-------------------------	-------

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	28787
Date of Issue:	2018-04-16
Date Received:	2018-04-13
Date Tested:	2018-04-13
Date Completed:	2018-04-16
Next Due Date:	2018-06-15

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description	: Handheld Particle Counter
Manufacturer	: Hal Technology
Model No.	: Hal-HPC301
Serial No.	: 3011701019
Flow rate	: 0.1 cfm
Zero Count Test	: 0 count per 5 minutes
Equipment No.	: A-27-01

Test Conditions:

Room Temperature	: 17-22 degree Celsius
Relative Humidity	: 40-70%

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

Correlation Factor (CF)	1.168
-------------------------	-------

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	28392D
Date of Issue:	2018-02-20
Date Received:	2018-02-15
Date Tested:	2018-02-15
Date Completed:	2018-02-20
Next Due Date:	2018-04-19

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description : Handheld Particle Counter
 Manufacturer : Hal Technology
 Model No. : Hal-HPC301
 Serial No. : 3011701016
 Flow rate : 0.1 cfm
 Zero Count Test : 0 count per 5 minutes
 Equipment No. : A-27-03

Test Conditions:

Room Temperature : 17-22 degree Celsius
 Relative Humidity : 40-70%

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

Correlation Factor (CF)	1.176
-------------------------	-------

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	28787A
Date of Issue:	2018-04-16
Date Received:	2018-04-13
Date Tested:	2018-04-13
Date Completed:	2018-04-16
Next Due Date:	2018-06-15

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description : Handheld Particle Counter
 Manufacturer : Hal Technology
 Model No. : Hal-HPC301
 Serial No. : 3011701016
 Flow rate : 0.1 cfm
 Zero Count Test : 0 count per 5 minutes
 Equipment No. : A-27-03

Test Conditions:

Room Temperature : 17-22 degree Celsius
 Relative Humidity : 40-70%

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

Correlation Factor (CF)	1.203
-------------------------	-------

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	28392A
Date of Issue:	2018-02-20
Date Received:	2018-02-15
Date Tested:	2018-02-15
Date Completed:	2018-02-20
Next Due Date:	2018-04-19

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description : Handheld Particle Counter
 Manufacturer : Hal Technology
 Model No. : Hal-HPC301
 Serial No. : 3011701017
 Flow rate : 0.1 cfm
 Zero Count Test : 0 count per 5 minutes
 Equipment No. : A-27-04

Test Conditions:

Room Temperature : 17-22 degree Celsius
 Relative Humidity : 40-70%

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

Correlation Factor (CF)	1.233
-------------------------	-------

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	28788
Date of Issue:	2018-04-16
Date Received:	2018-04-13
Date Tested:	2018-04-13
Date Completed:	2018-04-16
Next Due Date:	2018-06-15

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description : Handheld Particle Counter
 Manufacturer : Hal Technology
 Model No. : Hal-HPC301
 Serial No. : 3011701017
 Flow rate : 0.1 cfm
 Zero Count Test : 0 count per 5 minutes
 Equipment No. : A-27-04

Test Conditions:

Room Temperature : 17-22 degree Celsius
 Relative Humidity : 40-70%

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

Correlation Factor (CF)	1.158
-------------------------	-------

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	28392B
Date of Issue:	2018-02-20
Date Received:	2018-02-15
Date Tested:	2018-02-15
Date Completed:	2018-02-20
Next Due Date:	2018-04-19

ATTN: Mr. W. K. Tang

Page: 1 of 1

Certificate of Calibration

Item for Calibration:

Description	: Handheld Particle Counter
Manufacturer	: Hal Technology
Model No.	: Hal-HPC301
Serial No.	: 3011701012
Flow rate	: 0.1 cfm
Zero Count Test	: 0 count per 5 minutes
Equipment No.	: A-27-07

Test Conditions:

Room Temperature	: 17-22 degree Celsius
Relative Humidity	: 40-70%

Test Specifications & Methodology:

1. Instruction and Operation Manual High Volume Sampler, Andersen Samplers, Inc.
2. In-house method in according to the instruction manual: The Dust Monitor was compared with a calibrated High Volume Sampler and the result was used to generate the Correlation Factor (CF) between the Dust Monitor and High Volume Sampler.

Results:

Correlation Factor (CF)	1.161
-------------------------	-------

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE

Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	C/N/170915A
Date of Issue:	2017-09-18
Date Received:	2017-09-15
Date Tested:	2017-09-15
Date Completed:	2017-09-18
Next Due Date:	2018-09-17

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

Description : 'SVANTEK' Integrating Sound Level Meter
Manufacturer : SVANTEK
Model No. : SVAN 955
Serial No. : 12563
Microphone No. : 34377
Equipment No. : N-08-03

Test conditions:

Room Temperature : 22 degree Celsius
Relative Humidity : 60%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:


In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	C/N/170825
Date of Issue:	2017-08-28
Date Received:	2017-08-25
Date Tested:	2017-08-25
Date Completed:	2017-08-28
Next Due Date:	2018-08-27

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 957
Serial No.	: 21455
Microphone No.	: 43730
Equipment No.	: N-08-07

Test conditions:

Room Temperature	: 23 degree Celsius
Relative Humidity	: 60 %

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	C/N/170818
Date of Issue:	2017-08-21
Date Received:	2017-08-18
Date Tested:	2017-08-18
Date Completed:	2017-08-21
Next Due Date:	2018-08-20

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

Description : 'SVANTEK' Integrating Sound Level Meter
 Manufacturer : SVANTEK
 Model No. : SVAN 957
 Serial No. : 21459
 Microphone No. : 43676
 Equipment No. : N-08-08

Test conditions:

Room Temperature : 22 degree Celsius
 Relative Humidity : 61 %

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	C/N/170818A
Date of Issue:	2017-08-21
Date Received:	2017-08-18
Date Tested:	2017-08-18
Date Completed:	2017-08-21
Next Due Date:	2018-08-20

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 957
Serial No.	: 21460
Microphone No.	: 43679
Equipment No.	: N-08-09

Test conditions:

Room Temperature	: 22 degree Celsius
Relative Humidity	: 61 %

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	C/N/171215A
Date of Issue:	2017-12-18
Date Received:	2017-12-15
Date Tested:	2017-12-15
Date Completed:	2017-12-18
Next Due Date:	2018-12-17

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

Description	: Sound & Vibration Analyser
Manufacturer	: BSWA
Model No.	: BSWA 801
Serial No.	: 35921
Equipment No.	: N-13-02

Test conditions:

Room Temperature	: 20 degree Celsius
Relative Humidity	: 64%

Test Specifications:

Performance checking at 94 and 114 dB

Methodology:

In-house method, according to manufacturer instruction manual

Results:

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE

Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	C/N/170929
Date of Issue:	2017-09-30
Date Received:	2017-09-29
Date Tested:	2017-09-29
Date Completed:	2017-09-30
Next Due Date:	2018-09-29

ATTN: Mr. W.K. Tang

Page: 1 of 1

Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: SVANTEK
Model No.	: SV30A
Serial No.	: 24803
Equipment No.	: N-09-03

Test conditions:

Room Temperature	: 21 degree Celsius
Relative Humidity	: 60 %

Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	C/N/170929B
Date of Issue:	2017-09-30
Date Received:	2017-09-29
Date Tested:	2017-09-29
Date Completed:	2017-09-30
Next Due Date:	2018-09-29

ATTN: Mr. W.K. Tang

Page: 1 of 1

Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: SVANTEK
Model No.	: SV30A
Serial No.	: 24780
Equipment No.	: N-09-05

Test conditions:

Room Temperature	: 21 degree Celsius
Relative Humidity	: 60 %

Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	C/N/171103
Date of Issue:	2017-11-06
Date Received:	2017-11-03
Date Tested:	2017-11-03
Date Completed:	2017-11-06
Next Due Date:	2018-11-05

ATTN: Mr. W.K. Tang

Page: 1 of 1

Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: Brüel & Kjær
Model No.	: 4231
Serial No.	: 2326353
Equipment No.	: N-02-01

Test conditions:

Room Temperature	: 21 degree Celsius
Relative Humidity	: 64 %

Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
Room 1710, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong

Test Report No.:	C/N/170818C
Date of Issue:	2017-08-21
Date Received:	2017-08-18
Date Tested:	2017-08-18
Date Completed:	2017-08-21
Next Due Date:	2018-08-20

ATTN: Mr. W.K. Tang

Page: 1 of 1

Certificate of Calibration

Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: Brüel & Kjær
Model No.	: 4231
Serial No.	: 2412367
Equipment No.	: N-02-03

Test conditions:

Room Temperature	: 22 degree Celsius
Relative Humidity	: 61 %

Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE

Laboratory Manager

CALIBRATION CERTIFICATE

Calibration Item: Minimate Plus Unit (Calibration with Geophone
BG14847)
Model No.: 716A0403
Serial No.: BE17904
Calibration Date: 9 April 2018
Next Calibration Date: 9 April 2019
Method Used: In-house Method B3-001
In-house Testing Procedure No.: B3-001

<u>Test References</u>	<u>Model</u>	<u>Serial No.</u>
Blastmate III	714A0801	BA15521
ISEE Triaxial Geophone	714A9701	BG14463
GLOBAL SPECIALISTS 3MHz*	2030	256812
Stanford Spectrum Analyzer	SR760	41550
Aglient Multimeter*	34410A	MY47011119
HP Distortion Meter*	339A	810699
Bruel & Kjaer Accelerometer*	4370	30323
Bruel & Kjaer Charge Amplifier*	2647	2518810
Bruel & Kjaer Conditional Amplifier*	269	2152173
LDS Air Cooled Vibrator	V556	92794/1
LDS Field Power Supply	FPS10L	ARA 04/05
LDS Power Amplifier	PA1000L	ARA 07/06

*References are traceable to NIST or equivalent.

INSTANTEL INC. hereby certifies that this unit has been calibrated and that the results are consistent with the specifications published regarding this instrument. The SENSORCHECK feature of the unit is sufficiently reliable to indicate proper operation, although it is recommended that this unit be sent to INSTANTEL or an authorized service center for regular calibration.

Authorized by: _____


(Wong, Keefe Solomon)

Date: 9 April 2018

CALIBRATION CERTIFICATE

Calibration Item: Minimate Plus Unit (Calibration with Geophone
BG20674)
Model No.: 716A0403
Serial No.: BE17902
Calibration Date: 10 April 2018
Next Calibration Date: 10 April 2019
Method Used: In-house Method B3-001
In-house Testing Procedure No.: B3-001

<u>Test References</u>	<u>Model</u>	<u>Serial No.</u>
Blastmate III	714A0801	BA15521
ISEE Triaxial Geophone	714A9701	BG14463
GLOBAL SPECIALISTS 3MHz*	2030	256812
Stanford Spectrum Analyzer	SR760	41550
Aglient Multimeter*	34410A	MY47011119
HP Distortion Meter*	339A	810699
Bruel & Kjaer Accelerometer*	4370	30323
Bruel & Kjaer Charge Amplifier*	2647	2518810
Bruel & Kjaer Conditional Amplifier*	269	2152173
LDS Air Cooled Vibrator	V556	92794/1
LDS Field Power Supply	FPS10L	ARA 04/05
LDS Power Amplifier	PA1000L	ARA 07/06

*References are traceable to NIST or equivalent.

INSTANTEL INC. hereby certifies that this unit has been calibrated and that the results are consistent with the specifications published regarding this instrument. The SENSORCHECK feature of the unit is sufficiently reliable to indicate proper operation, although it is recommended that this unit be sent to INSTANTEL or an authorized service center for regular calibration.

Authorized by: _____



(Wong, Keefe Solomon)

Date: 10 April 2018

CALIBRATION CERTIFICATE

Calibration Item: Minimate Plus Unit (Calibration with Geophone
BG16957)
Model No.: 716A0403
Serial No.: BE17505
Calibration Date: 22 March 2018
Next Calibration Date: 22 March 2019
Method Used: In-house Method B3-001
In-house Testing Procedure No.: B3-001

<u>Test References</u>	<u>Model</u>	<u>Serial No.</u>
Blastmate III	714A0801	BA15521
ISEE Triaxial Geophone	714A9701	BG14463
GLOBAL SPECIALISTS 3MHz*	2030	256812
Stanford Spectrum Analyzer	SR760	41550
Aglient Multimeter*	34410A	MY47011119
HP Distortion Meter*	339A	810699
Bruel & Kjaer Accelerometer*	4370	30323
Bruel & Kjaer Charge Amplifier*	2647	2518810
Bruel & Kjaer Conditional Amplifier*	269	2152173
LDS Air Cooled Vibrator	V556	92794/1
LDS Field Power Supply	FPS10L	ARA 04/05
LDS Power Amplifier	PA1000L	ARA 07/06

*References are traceable to NIST or equivalent.

INSTANTEL INC. hereby certifies that this unit has been calibrated and that the results are consistent with the specifications published regarding this instrument. The SENSORCHECK feature of the unit is sufficiently reliable to indicate proper operation, although it is recommended that this unit be sent to INSTANTEL or an authorized service center for regular calibration.

Authorized by: _____

(Leung Man Hin, Eric)

Date: 22 March 2018



CERTIFICATE OF CALIBRATION

Calibration Date: 1st September 2017

Model: iCivil-1011 Inclinometer

Serial No. : HK110118

Method Used: By direct measurement

Laboratory Conditions:

Ambient Temperature: (23±2)°C

Relative Humidity: (50 ±20)%

Test Reference

Dual-Axis Digital Angle Protractor

Model

TLL-90S

Equipment ID

EPC001

Calibration Result

X-Axis Measurement

Applied Angle (degree)	UUT Reading (degree)	Error (degree)
10.011	9.943	-0.068
5.005	4.976	-0.029
1.003	0.995	-0.008
0.001	-0.002	-0.003
-1.005	-0.996	0.009
-5.015	-4.976	0.039
-10.009	-9.940	0.069

Remarks:

1. The above calibration data applies only to the instrument described above.

Checked By:

Date: 1st September 2017

*** End of Report***



CERTIFICATE OF CALIBRATION

Calibration Date: 1st September 2017

Model: iCivil-1011 Inclinometer

Serial No. : HK110120

Method Used: By direct measurement

Laboratory Conditions:

Ambient Temperature: (23±2)°C

Relative Humidity: (50 ±20)%

Test Reference

Dual-Axis Digital Angle Protractor

Model

TLL-90S

Equipment ID

EPC001

Calibration Result

X-Axis Measurement

Applied Angle (degree)	UUT Reading (degree)	Error (degree)
10.005	9.945	-0.06
5.007	4.978	-0.029
1.003	0.998	-0.005
0.001	-0.001	-0.002
-1.008	-0.998	0.01
-5.010	-4.974	0.036
-10.001	-9.943	0.058

Remarks:

1. The above calibration data applies only to the instrument described above.

Checked By:

Date: 1st September 2017

*** End of Report***



YSF Corporation Limited

5/A., Blk 1 Kin Ho Ind Bldg 20-24, Au Pui Wan St,
Fo Tan, Shatin, N.T. Hong Kong

Phone: 852-8109 8368 Fax: 852-3007 4857

CERTIFICATE OF CALIBRATION

Certificate No.	: CS-CC- 170820	Customer	: Leighton-China State Joint Venture
Manufacturer	: Leica	Address	: 39/F., Sun Hung Kai Centre, 30 Harbour Road, Hong Kong
Equipment	: Digital Level	Calibration Interval	: 12 months
Model	: LS15 0.3mm	Reference Document	: CS/ME/ 3(HKST)
Serial No.	: 701133	Report No.	: CS-CR- 170820
Calibration Date	: 14th September, 2017		
Expire Date	: 13th September, 2018		

The instrument has been checked and calibrated according to document procedures and using standards and instruments which are traceable to international accepted standards. The standards and instruments used in the calibration are calibrated on a schedule which is adjusted to maintain traceability at the required accuracy level, or have been derived from the ratio type of self-calibration techniques. This is established by our Quality Management System, audited to ISO9001 :2008 by an independent national accredited body.

The specified calibration interval is a recommendation. Depending on the type of use ambient conditions or accuracy requirements, other calibration intervals may be applicable. The user shall be responsible that calibration is carried out at adequate intervals.

YSF Corporation Ltd. hereby certifies this instrument meets or exceeds all published specifications of the manufacturer at present inforce. This calibration certificate may only be distributed in a complete and unchanged form. Unsigned calibration certificates are invalid.

Calibrated by

Wayne

Wayne Ng, Service Engineer
14th September, 2017

CKL/CSL/170820

Checked by



Wallace Yu, Service Manager
14th September, 2017



YSF Corporation Ltd.

Calibration Report

Certificate No. : CS-CC-170820 Certificate Report No. : CS-CR-170820

Client : Leighton-China State Joint Venture

Address : 39/F., Sun Hung Kai Centre, 30 Harbour Road, Hong Kong

Item Calibrated : **Name/Description:** Digital Level

Manufacturer: Leica

Model: LS15 0.3mm **Eqt. No:** 701133

Reference Standard : 5198266

Calibration check according to customer's requirement.

Calibration Method : Procedure CS02

Calibration Conditions

Temperature : ($31 \pm 3^{\circ}\text{C}$)

Relative Humidity : 84% RH

Date of Test : 14th September, 2017

Test Results : **PASS** (All calibration points were within the tolerances as shown in the attached calibration results.)

Calibrated by : Wayne
Wayne Ng, Service Engineer
Date: 14th September, 2017

HKCS Approved Signatory: [Signature]
Wallace Yu, Service Manager
Date: 14th September, 2017

- Notes:
- 1, The test equipment used for calibration are traceable to national standards/international system of units(SI)
 - 2, The values given in this calibration certificate only to the values measured at the time of test & any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. YSF Corporation Ltd. shall not be liable for any loss/damage resulting from the use of the equipment.
 - 3, The test results apply to the above Unit-Under-Test only.
 - 4, This certificate shall not be reproduced, except on full, without approval of YSF Corporation Ltd.
-



YSF Corporation Ltd.

Calibration Report

Certificate Report No.:CS-CR-170820

Certificate No. :CS-CC-170820

Client : Leighton-China State Joint Venture

Address : 39/F., Sun Hung Kai Centre, 30 Harbour Road, Hong Kong

Item Calibrated :Name/Description: Digital Level

Manufacturer: Leica

Model: LS15 0.3mm

Eqt. No: 701133

Inspection Item	Result
Line of sight leveling	Pass
Compensation accuracy	Pass
Stadia spacing	Pass
Circular bubble level accuracy	Pass
Focusing	Pass
Hori. Motion	Pass

Overall Inspection Result : PASS

Served by :

Wayne

Wayne Ng, Service Engineer

Date: 14th September, 2017

We hereby confirm the inspection has been completed and complied with the specifications required.

YSF Corporation Ltd.

Wallace Yu
Wallace Yu, Service Manager

Date: 14th September, 2017



The Safety Company

MSA Corporate Center • 1000 Cranberry Woods Drive • Cranberry Township, PA 16066

www.msasafety.com

Telephone: (800) MSA-2222

ALTAIR5X
CERTIFICATE OF CALIBRATION

Serial Number: 120848

Part Number: A-ALT5X-A-N-K-D-1-0-0-T-0-0-0

Sales Order Number:



Factory Calibration Date: 08/18/17

Set Points

	METHANE 0-100.00 %LEL	O2 0-30.00 %VOL	CO 0-2000.00 PPM	H2S 0-200.00 PPM	NH3 0-100.00 PPM	
↓ (Low)	10.00 %LEL	19.50 %VOL	25.00 PPM	10.00 PPM	25.00 PPM	
↑ (High)	20.00 %LEL	23.00 %VOL	100.00 PPM	15.00 PPM	50.00 PPM	
STEL			100.00 PPM	15.00 PPM	35.00 PPM	
TWA			25.00 PPM	10.00 PPM	25.00 PPM	
Calibrated Value	Methane 1.45 %VOL	O2 15.00 %VOL	CO 60.4 PPM	H2S 21.0 PPM	NH3 25 PPM	
Cylinder Lot #	1027601826B	1027601826B	1027601826B	1027601826B	201397	

All applicable inspections, testing, and calibrations were performed using NIST traceable equipment, where available, in accordance with MSA's ISO 9001 Certified Quality System. Each material, component, and/or instrument must be installed, operated and maintained in strict accordance with its labels, cautions, warnings, instructions, and within the limitations stated in the supplied instruction manual. Routine calibration checks, equipment inspections, and applicable preventative maintenance measures must be performed to verify that the materials, components, and/or instruments are operating properly. Failure to perform these tasks on a routine basis, or suggested intervals, with specified equipment or methods, may result in inaccurate readings.

Process Certified By:

Calibrated By: E. Weber

JIM HOFFMAN
QUALITY ENGINEER

LOCATION: 1000 Cranberry Woods Drive • Cranberry Township, PA 16066-5296



The Safety Company

MSA Corporate Center • 1000 Cranberry Woods Drive • Cranberry Township, PA 16066

www.msasafety.com

Telephone: (800) MSA-2222

ALTAIR5X CERTIFICATE OF CALIBRATION

Serial Number: 120847

Part Number: A-ALT5X-A-N-K-D-1-0-0-T-0-0-0

Sales Order Number:



Factory Calibration Date: 08/18/17

Set Points

↓ (Low)						
↑ (High)						
STEL						
TWA						
Calibrated Value	Methane 1.45 %VOL	O2 15.00 %VOL	CO 60.4 PPM	H2S 21.0 PPM	NH3 25 PPM	
Cylinder Lot #	1027601826B	1027601826B	1027601826B	1027601826B	201397	

All applicable inspections, testing, and calibrations were performed using NIST traceable equipment, where available, in accordance with MSA's ISO 9001 Certified Quality System. Each material, component, and/or instrument must be installed, operated and maintained in strict accordance with its labels, cautions, warnings, instructions, and within the limitations stated in the supplied instruction manual. Routine calibration checks, equipment inspections, and applicable preventative maintenance measures must be performed to verify that the materials, components, and/or instruments are operating properly. Failure to perform these tasks on a routine basis, or suggested intervals, with specified equipment or methods, may result in inaccurate readings.

Process Certified By:

Calibrated By: E. Weber

JIM HOFFMAN
QUALITY ENGINEER

LOCATION: 1000 Cranberry Woods Drive • Cranberry Township, PA 16066-5296

APPENDIX C
WEATHER INFORMATION

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

I. General Information

Date	Mean Air Temperature (°C)	Mean Relative Humidity (%)	Precipitation (mm)
1 April 2018	21.3 – 27.9	73	-
2 April 2018	21.5 – 28.7	71	-
3 April 2018	21.9 – 29.4	74	-
4 April 2018	22.6 – 28.5	78	-
5 April 2018	22.7 – 27.8	78	-
6 April 2018	17.5 – 26.6	70	Trace
7 April 2018	16.1 – 20.3	45	Trace
8 April 2018	16.3 – 24.9	53	-
9 April 2018	19.0 – 26.5	75	-
10 April 2018	21.1 – 28.5	78	-
11 April 2018	22.5 – 27.6	83	-
12 April 2018	23.9 – 28.1	82	-
13 April 2018	24.6 – 30.6	79	Trace
14 April 2018	25.2 – 29.9	79	Trace
15 April 2018	18.6 – 25.7	85	17.2
16 April 2018	17.5 – 19.4	88	2.0
17 April 2018	17.4 – 22.9	82	0.2
18 April 2018	21.1 – 25.6	78	0.1
19 April 2018	21.4 – 26.3	76	-

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

I. General Information

Date	Mean Air Temperature (°C)	Mean Relative Humidity (%)	Precipitation (mm)
20 April 2018	22.5 – 26.2	83	Trace
21 April 2018	23.0 – 27.5	83	Trace
22 April 2018	23.7 – 29.0	86	Trace
23 April 2018	24.3 – 30.2	79	Trace
24 April 2018	23.9 – 26.7	85	8.2
25 April 2018	23.3 – 24.7	79	Trace
26 April 2018	22.7 – 24.6	84	0.3
27 April 2018	22.9 – 28.5	80	Trace
28 April 2018	23.1 – 26.4	84	0.1
29 April 2018	23.9 – 29.3	82	Trace
30 April 2018	24.6 – 29.2	85	Trace

* The above information was extracted from the daily weather summary by Hong Kong Observatory.

** Trace means rainfall less than 0.05 mm

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

Date	Time	Wind Speed m/s	Direction
1-Apr-2018	00:00	1.9	WNW
1-Apr-2018	01:00	1.9	WNW
1-Apr-2018	02:00	2.2	WNW
1-Apr-2018	03:00	2	WNW
1-Apr-2018	04:00	1.9	WNW
1-Apr-2018	05:00	2.6	WNW
1-Apr-2018	06:00	2.3	W
1-Apr-2018	07:00	3	W
1-Apr-2018	08:00	2.5	WNW
1-Apr-2018	09:00	3	WNW
1-Apr-2018	10:00	2.2	WNW
1-Apr-2018	11:00	2.9	W
1-Apr-2018	12:00	2.8	WNW
1-Apr-2018	13:00	3.1	WNW
1-Apr-2018	14:00	3.2	WNW
1-Apr-2018	15:00	2.8	WNW
1-Apr-2018	16:00	3	W
1-Apr-2018	17:00	2.8	W
1-Apr-2018	18:00	2.6	W
1-Apr-2018	19:00	2.4	WSW
1-Apr-2018	20:00	2.8	SSW
1-Apr-2018	21:00	2.7	SSW
1-Apr-2018	22:00	2.7	W
1-Apr-2018	23:00	2.8	WNW
2-Apr-2018	00:00	3.2	WNW
2-Apr-2018	01:00	2.8	W
2-Apr-2018	02:00	2.6	NE
2-Apr-2018	03:00	2.5	ESE
2-Apr-2018	04:00	2.4	NW
2-Apr-2018	05:00	2.2	NNE
2-Apr-2018	06:00	1.6	NNE
2-Apr-2018	07:00	2.2	NE
2-Apr-2018	08:00	2.1	E
2-Apr-2018	09:00	1.8	E
2-Apr-2018	10:00	2	ENE
2-Apr-2018	11:00	2.5	E
2-Apr-2018	12:00	2.7	NE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

2-Apr-2018	13:00	2.4	WSW
2-Apr-2018	14:00	2.6	WNW
2-Apr-2018	15:00	2.4	W
2-Apr-2018	16:00	2.1	SW
2-Apr-2018	17:00	2.2	SW
2-Apr-2018	18:00	2.1	SSW
2-Apr-2018	19:00	2.2	SW
2-Apr-2018	20:00	2.1	WSW
2-Apr-2018	21:00	2.2	SW
2-Apr-2018	22:00	1.9	SW
2-Apr-2018	23:00	1.5	WNW
3-Apr-2018	00:00	1.6	S
3-Apr-2018	01:00	2.2	S
3-Apr-2018	02:00	2	SSW
3-Apr-2018	03:00	2	SSW
3-Apr-2018	04:00	2.2	S
3-Apr-2018	05:00	2.2	SSW
3-Apr-2018	06:00	1.5	WNW
3-Apr-2018	07:00	2.5	W
3-Apr-2018	08:00	2.4	WNW
3-Apr-2018	09:00	2.3	WNW
3-Apr-2018	10:00	2.5	WNW
3-Apr-2018	11:00	3	WNW
3-Apr-2018	12:00	3.2	W
3-Apr-2018	13:00	2.9	SE
3-Apr-2018	14:00	3.3	SSW
3-Apr-2018	15:00	3.5	WNW
3-Apr-2018	16:00	2.3	WNW
3-Apr-2018	17:00	1.8	WNW
3-Apr-2018	18:00	1.8	WNW
3-Apr-2018	19:00	1.8	WNW
3-Apr-2018	20:00	1.4	WNW
3-Apr-2018	21:00	1.7	WNW
3-Apr-2018	22:00	1.5	WNW
3-Apr-2018	23:00	1.4	SSW
4-Apr-2018	00:00	1.5	SSW
4-Apr-2018	01:00	1.6	WSW
4-Apr-2018	02:00	1.9	WNW

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

4-Apr-2018	03:00	1.6	WNW
4-Apr-2018	04:00	1.4	WNW
4-Apr-2018	05:00	1.8	W
4-Apr-2018	06:00	1.4	SW
4-Apr-2018	07:00	1.4	SW
4-Apr-2018	08:00	1.5	SW
4-Apr-2018	09:00	1.5	SW
4-Apr-2018	10:00	1.9	WSW
4-Apr-2018	11:00	2.6	SW
4-Apr-2018	12:00	2.8	W
4-Apr-2018	13:00	3.2	WSW
4-Apr-2018	14:00	3	WSW
4-Apr-2018	15:00	3	WSW
4-Apr-2018	16:00	2.8	WNW
4-Apr-2018	17:00	2.1	W
4-Apr-2018	18:00	1.7	WSW
4-Apr-2018	19:00	1.8	WSW
4-Apr-2018	20:00	2	SW
4-Apr-2018	21:00	1.8	WSW
4-Apr-2018	22:00	2.1	WSW
4-Apr-2018	23:00	2	WSW
5-Apr-2018	00:00	1.8	WSW
5-Apr-2018	01:00	1.5	WSW
5-Apr-2018	02:00	1.7	SW
5-Apr-2018	03:00	2	WNW
5-Apr-2018	04:00	1.9	W
5-Apr-2018	05:00	1.4	WNW
5-Apr-2018	06:00	2	WSW
5-Apr-2018	07:00	1.4	SSW
5-Apr-2018	08:00	1.7	SW
5-Apr-2018	09:00	2.1	SW
5-Apr-2018	10:00	2.1	SW
5-Apr-2018	11:00	1.6	WSW
5-Apr-2018	12:00	1.9	SW
5-Apr-2018	13:00	2.1	SW
5-Apr-2018	14:00	2.1	W
5-Apr-2018	15:00	2.9	W
5-Apr-2018	16:00	2.5	W

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

5-Apr-2018	17:00	2.1	W
5-Apr-2018	18:00	2.6	W
5-Apr-2018	19:00	1.8	WNW
5-Apr-2018	20:00	1.9	WNW
5-Apr-2018	21:00	1.5	WNW
5-Apr-2018	22:00	2.1	W
5-Apr-2018	23:00	1.8	W
6-Apr-2018	00:00	1.9	W
6-Apr-2018	01:00	1.9	WNW
6-Apr-2018	02:00	1.4	WNW
6-Apr-2018	03:00	1.5	WSW
6-Apr-2018	04:00	1.4	W
6-Apr-2018	05:00	1.1	WNW
6-Apr-2018	06:00	1	WNW
6-Apr-2018	07:00	0.9	W
6-Apr-2018	08:00	1.1	WSW
6-Apr-2018	09:00	1.3	W
6-Apr-2018	10:00	1.4	W
6-Apr-2018	11:00	1.6	W
6-Apr-2018	12:00	1.5	WNW
6-Apr-2018	13:00	2.3	WNW
6-Apr-2018	14:00	2.3	WNW
6-Apr-2018	15:00	2.1	WNW
6-Apr-2018	16:00	2.6	NW
6-Apr-2018	17:00	1.9	W
6-Apr-2018	18:00	1.8	W
6-Apr-2018	19:00	1.5	WNW
6-Apr-2018	20:00	1.5	WNW
6-Apr-2018	21:00	0.9	W
6-Apr-2018	22:00	1	SSW
6-Apr-2018	23:00	0.8	SSW
7-Apr-2018	00:00	1	SSW
7-Apr-2018	01:00	0.8	SW
7-Apr-2018	02:00	0.8	SSW
7-Apr-2018	03:00	0.6	ESE
7-Apr-2018	04:00	0.4	WSW
7-Apr-2018	05:00	0.5	SW
7-Apr-2018	06:00	0.6	SSE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

7-Apr-2018	07:00	0.5	ESE
7-Apr-2018	08:00	0.5	ENE
7-Apr-2018	09:00	0.9	SSE
7-Apr-2018	10:00	1.6	SSE
7-Apr-2018	11:00	1.7	E
7-Apr-2018	12:00	2.5	ESE
7-Apr-2018	13:00	2.3	ENE
7-Apr-2018	14:00	2.2	NE
7-Apr-2018	15:00	1.9	SSE
7-Apr-2018	16:00	1.6	SSE
7-Apr-2018	17:00	2	E
7-Apr-2018	18:00	1.3	E
7-Apr-2018	19:00	0.9	E
7-Apr-2018	20:00	0.6	NE
7-Apr-2018	21:00	0.7	NE
7-Apr-2018	22:00	0.8	N
7-Apr-2018	23:00	0.7	NNE
8-Apr-2018	00:00	0.8	NE
8-Apr-2018	01:00	1	NE
8-Apr-2018	02:00	1	NE
8-Apr-2018	03:00	0.8	N
8-Apr-2018	04:00	0.8	NNE
8-Apr-2018	05:00	1	E
8-Apr-2018	06:00	1	NE
8-Apr-2018	07:00	0.9	ENE
8-Apr-2018	08:00	1.3	ENE
8-Apr-2018	09:00	1.4	ENE
8-Apr-2018	10:00	2.1	NE
8-Apr-2018	11:00	2.2	N
8-Apr-2018	12:00	2	NE
8-Apr-2018	13:00	2.1	NNE
8-Apr-2018	14:00	2	NE
8-Apr-2018	15:00	2.4	N
8-Apr-2018	16:00	1.7	E
8-Apr-2018	17:00	2.5	ENE
8-Apr-2018	18:00	1.9	S
8-Apr-2018	19:00	2.1	N
8-Apr-2018	20:00	1.9	NW

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

8-Apr-2018	21:00	2.1	NW
8-Apr-2018	22:00	2	WNW
8-Apr-2018	23:00	2.1	W
9-Apr-2018	00:00	2	WNW
9-Apr-2018	01:00	2.4	WNW
9-Apr-2018	02:00	1.9	WNW
9-Apr-2018	03:00	1.8	SW
9-Apr-2018	04:00	1.3	W
9-Apr-2018	05:00	1.2	WSW
9-Apr-2018	06:00	1.1	SW
9-Apr-2018	07:00	1.3	W
9-Apr-2018	08:00	2.1	WNW
9-Apr-2018	09:00	2.8	W
9-Apr-2018	10:00	2.8	WNW
9-Apr-2018	11:00	2.9	WNW
9-Apr-2018	12:00	3.2	WSW
9-Apr-2018	13:00	2.5	SW
9-Apr-2018	14:00	2.1	SE
9-Apr-2018	15:00	2.5	N
9-Apr-2018	16:00	2.5	E
9-Apr-2018	17:00	2.5	ENE
9-Apr-2018	18:00	1.9	ENE
9-Apr-2018	19:00	1.5	ENE
9-Apr-2018	20:00	1	E
9-Apr-2018	21:00	1.6	ENE
9-Apr-2018	22:00	1.6	NE
9-Apr-2018	23:00	1.6	ENE
10-Apr-2018	00:00	1.6	NE
10-Apr-2018	01:00	1.5	NE
10-Apr-2018	02:00	1.5	NNE
10-Apr-2018	03:00	2	N
10-Apr-2018	04:00	1.6	ESE
10-Apr-2018	05:00	1.5	ENE
10-Apr-2018	06:00	0.8	ENE
10-Apr-2018	07:00	0.9	ENE
10-Apr-2018	08:00	1.3	N
10-Apr-2018	09:00	1.6	NNE
10-Apr-2018	10:00	2.3	N

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

10-Apr-2018	11:00	2.4	ENE
10-Apr-2018	12:00	2.8	N
10-Apr-2018	13:00	2.8	SW
10-Apr-2018	14:00	1.9	SSE
10-Apr-2018	15:00	1.6	E
10-Apr-2018	16:00	1.7	NNE
10-Apr-2018	17:00	1.6	N
10-Apr-2018	18:00	1.2	NNE
10-Apr-2018	19:00	0.8	NNE
10-Apr-2018	20:00	1.3	E
10-Apr-2018	21:00	0.9	E
10-Apr-2018	22:00	1.1	ENE
10-Apr-2018	23:00	0.8	ENE
11-Apr-2018	00:00	1.6	NE
11-Apr-2018	01:00	0.8	ENE
11-Apr-2018	02:00	0.8	ENE
11-Apr-2018	03:00	0.7	ENE
11-Apr-2018	04:00	1.4	NNE
11-Apr-2018	05:00	1.2	ENE
11-Apr-2018	06:00	1.6	SE
11-Apr-2018	07:00	1.4	ENE
11-Apr-2018	08:00	1.4	ENE
11-Apr-2018	09:00	2.3	ENE
11-Apr-2018	10:00	2	ENE
11-Apr-2018	11:00	2.2	ESE
11-Apr-2018	12:00	1.9	ESE
11-Apr-2018	13:00	2.2	ESE
11-Apr-2018	14:00	2.6	ENE
11-Apr-2018	15:00	2.6	NE
11-Apr-2018	16:00	1.9	NE
11-Apr-2018	17:00	2.2	ESE
11-Apr-2018	18:00	1.9	ESE
11-Apr-2018	19:00	1.4	ENE
11-Apr-2018	20:00	1.5	ESE
11-Apr-2018	21:00	1.4	ENE
11-Apr-2018	22:00	1	ENE
11-Apr-2018	23:00	1.2	SSE
12-Apr-2018	00:00	1.2	S

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

12-Apr-2018	01:00	1.3	SE
12-Apr-2018	02:00	1.1	SE
12-Apr-2018	03:00	1.3	SE
12-Apr-2018	04:00	1.6	ESE
12-Apr-2018	05:00	1.8	SE
12-Apr-2018	06:00	1.4	ENE
12-Apr-2018	07:00	1.4	ESE
12-Apr-2018	08:00	2	SSE
12-Apr-2018	09:00	2.3	SE
12-Apr-2018	10:00	2.4	ENE
12-Apr-2018	11:00	2.5	NE
12-Apr-2018	12:00	3.4	NE
12-Apr-2018	13:00	3.3	NE
12-Apr-2018	14:00	3	SE
12-Apr-2018	15:00	2.9	SSW
12-Apr-2018	16:00	2.7	SSW
12-Apr-2018	17:00	2.6	ESE
12-Apr-2018	18:00	2.3	SE
12-Apr-2018	19:00	2.6	SE
12-Apr-2018	20:00	2.4	E
12-Apr-2018	21:00	1.9	NE
12-Apr-2018	22:00	1.9	ESE
12-Apr-2018	23:00	2.2	N
13-Apr-2018	00:00	2.4	ESE
13-Apr-2018	01:00	2.5	ESE
13-Apr-2018	02:00	2	ESE
13-Apr-2018	03:00	1.9	SE
13-Apr-2018	04:00	1.6	ESE
13-Apr-2018	05:00	1.9	NE
13-Apr-2018	06:00	2.2	WSW
13-Apr-2018	07:00	1.9	WNW
13-Apr-2018	08:00	1.7	WSW
13-Apr-2018	09:00	2.2	NE
13-Apr-2018	10:00	2.7	ENE
13-Apr-2018	11:00	3.3	NNE
13-Apr-2018	12:00	4	NNE
13-Apr-2018	13:00	3.6	ENE
13-Apr-2018	14:00	3.5	ENE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

13-Apr-2018	15:00	3.3	NE
13-Apr-2018	16:00	2.6	ENE
13-Apr-2018	17:00	2.6	N
13-Apr-2018	18:00	2.7	ESE
13-Apr-2018	19:00	2.5	NE
13-Apr-2018	20:00	2.6	NNE
13-Apr-2018	21:00	2.8	NNE
13-Apr-2018	22:00	2.3	ENE
13-Apr-2018	23:00	2.5	ENE
14-Apr-2018	00:00	2.3	NE
14-Apr-2018	01:00	2	ENE
14-Apr-2018	02:00	2.2	E
14-Apr-2018	03:00	1.9	NNE
14-Apr-2018	04:00	1.8	NE
14-Apr-2018	05:00	2	NE
14-Apr-2018	06:00	1.6	NE
14-Apr-2018	07:00	2.1	ENE
14-Apr-2018	08:00	2.5	NE
14-Apr-2018	09:00	3.1	NE
14-Apr-2018	10:00	2.6	NE
14-Apr-2018	11:00	2.8	E
14-Apr-2018	12:00	2.4	ENE
14-Apr-2018	13:00	2.5	ENE
14-Apr-2018	14:00	2.2	ENE
14-Apr-2018	15:00	2.5	ENE
14-Apr-2018	16:00	2.3	ENE
14-Apr-2018	17:00	2	NE
14-Apr-2018	18:00	1.8	NNE
14-Apr-2018	19:00	2	NE
14-Apr-2018	20:00	1.9	NE
14-Apr-2018	21:00	2.2	N
14-Apr-2018	22:00	2.3	ENE
14-Apr-2018	23:00	2	S
15-Apr-2018	00:00	2.2	NE
15-Apr-2018	01:00	1.7	NE
15-Apr-2018	02:00	2	NE
15-Apr-2018	03:00	2.1	ENE
15-Apr-2018	04:00	1.9	NNE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

15-Apr-2018	05:00	1.7	NNE
15-Apr-2018	06:00	1.7	NNE
15-Apr-2018	07:00	2	NNE
15-Apr-2018	08:00	2.2	ENE
15-Apr-2018	09:00	2.1	SE
15-Apr-2018	10:00	2.4	SE
15-Apr-2018	11:00	2.2	SSE
15-Apr-2018	12:00	2.1	ESE
15-Apr-2018	13:00	1.7	ESE
15-Apr-2018	14:00	1.9	ESE
15-Apr-2018	15:00	2	ESE
15-Apr-2018	16:00	2.1	SE
15-Apr-2018	17:00	1.9	SSE
15-Apr-2018	18:00	1.8	NNE
15-Apr-2018	19:00	1.4	NE
15-Apr-2018	20:00	1.4	ENE
15-Apr-2018	21:00	1.4	NE
15-Apr-2018	22:00	1.4	ENE
15-Apr-2018	23:00	1.2	ENE
16-Apr-2018	00:00	1.5	ENE
16-Apr-2018	01:00	1.6	N
16-Apr-2018	02:00	1.4	ENE
16-Apr-2018	03:00	1.7	NE
16-Apr-2018	04:00	2	ENE
16-Apr-2018	05:00	2	E
16-Apr-2018	06:00	1.7	E
16-Apr-2018	07:00	2.1	E
16-Apr-2018	08:00	2.1	E
16-Apr-2018	09:00	2.3	S
16-Apr-2018	10:00	1.9	NE
16-Apr-2018	11:00	2	E
16-Apr-2018	12:00	2.5	ENE
16-Apr-2018	13:00	2.4	ENE
16-Apr-2018	14:00	2.4	ENE
16-Apr-2018	15:00	2.3	NE
16-Apr-2018	16:00	2.5	ENE
16-Apr-2018	17:00	2.6	N
16-Apr-2018	18:00	1.9	ENE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

16-Apr-2018	19:00	2.3	NE
16-Apr-2018	20:00	1.7	ENE
16-Apr-2018	21:00	1.9	ENE
16-Apr-2018	22:00	1.4	ENE
16-Apr-2018	23:00	1.9	N
17-Apr-2018	00:00	1.9	NE
17-Apr-2018	01:00	1.8	ENE
17-Apr-2018	02:00	1.5	ENE
17-Apr-2018	03:00	1.8	ENE
17-Apr-2018	04:00	1.4	E
17-Apr-2018	05:00	1.4	ENE
17-Apr-2018	06:00	1.8	NE
17-Apr-2018	07:00	1.7	NE
17-Apr-2018	08:00	1.5	SE
17-Apr-2018	09:00	1.8	NNE
17-Apr-2018	10:00	1.9	NNE
17-Apr-2018	11:00	2	ENE
17-Apr-2018	12:00	2.4	ENE
17-Apr-2018	13:00	1.8	ENE
17-Apr-2018	14:00	1.9	ESE
17-Apr-2018	15:00	2	ESE
17-Apr-2018	16:00	2	ESE
17-Apr-2018	17:00	1.4	SE
17-Apr-2018	18:00	1.1	ESE
17-Apr-2018	19:00	1.1	E
17-Apr-2018	20:00	1	NE
17-Apr-2018	21:00	1.2	N
17-Apr-2018	22:00	1.2	SE
17-Apr-2018	23:00	0.9	E
18-Apr-2018	00:00	1.1	N
18-Apr-2018	01:00	1.4	ENE
18-Apr-2018	02:00	1.1	N
18-Apr-2018	03:00	0.9	ENE
18-Apr-2018	04:00	0.9	ENE
18-Apr-2018	05:00	0.9	ENE
18-Apr-2018	06:00	1.1	ENE
18-Apr-2018	07:00	1.4	ESE
18-Apr-2018	08:00	1.6	NNE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

18-Apr-2018	09:00	2.6	ESE
18-Apr-2018	10:00	2.4	SSE
18-Apr-2018	11:00	2.4	ENE
18-Apr-2018	12:00	2.2	ENE
18-Apr-2018	13:00	2.3	NE
18-Apr-2018	14:00	2.3	SE
18-Apr-2018	15:00	2.2	SE
18-Apr-2018	16:00	2	NE
18-Apr-2018	17:00	1.6	NE
18-Apr-2018	18:00	1.6	ENE
18-Apr-2018	19:00	1.4	NE
18-Apr-2018	20:00	1.2	ENE
18-Apr-2018	21:00	1.3	ENE
18-Apr-2018	22:00	1.3	NE
18-Apr-2018	23:00	1.3	NE
19-Apr-2018	00:00	1.2	NE
19-Apr-2018	01:00	1.1	ENE
19-Apr-2018	02:00	0.9	ENE
19-Apr-2018	03:00	0.8	ESE
19-Apr-2018	04:00	0.8	ENE
19-Apr-2018	05:00	1	ENE
19-Apr-2018	06:00	0.8	ENE
19-Apr-2018	07:00	0.8	ENE
19-Apr-2018	08:00	1.4	NNE
19-Apr-2018	09:00	1.6	NE
19-Apr-2018	10:00	2.7	ENE
19-Apr-2018	11:00	3.1	ENE
19-Apr-2018	12:00	2.5	NE
19-Apr-2018	13:00	2.3	NE
19-Apr-2018	14:00	2.1	NW
19-Apr-2018	15:00	2.5	ENE
19-Apr-2018	16:00	2.6	ENE
19-Apr-2018	17:00	2.3	NE
19-Apr-2018	18:00	2	NNE
19-Apr-2018	19:00	1.5	E
19-Apr-2018	20:00	1	WNW
19-Apr-2018	21:00	0.8	SE
19-Apr-2018	22:00	1.1	SE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

19-Apr-2018	23:00	1.1	SE
20-Apr-2018	00:00	1	E
20-Apr-2018	01:00	1	NE
20-Apr-2018	02:00	0.8	SSE
20-Apr-2018	03:00	1	SSE
20-Apr-2018	04:00	0.8	ENE
20-Apr-2018	05:00	0.8	NE
20-Apr-2018	06:00	0.8	NNE
20-Apr-2018	07:00	1	ENE
20-Apr-2018	08:00	1.6	ENE
20-Apr-2018	09:00	2.5	NNE
20-Apr-2018	10:00	2.7	NE
20-Apr-2018	11:00	3	ENE
20-Apr-2018	12:00	2.8	NE
20-Apr-2018	13:00	3	ENE
20-Apr-2018	14:00	2.3	ENE
20-Apr-2018	15:00	1.8	NNE
20-Apr-2018	16:00	1.7	NE
20-Apr-2018	17:00	1.4	E
20-Apr-2018	18:00	0.9	E
20-Apr-2018	19:00	0.9	E
20-Apr-2018	20:00	0.8	E
20-Apr-2018	21:00	0.8	ENE
20-Apr-2018	22:00	0.9	E
20-Apr-2018	23:00	1	E
21-Apr-2018	00:00	1.5	ENE
21-Apr-2018	01:00	1.4	ENE
21-Apr-2018	02:00	1.4	E
21-Apr-2018	03:00	1.4	E
21-Apr-2018	04:00	1.4	N
21-Apr-2018	05:00	1.3	NE
21-Apr-2018	06:00	0.9	NNE
21-Apr-2018	07:00	0.8	NE
21-Apr-2018	08:00	0.9	E
21-Apr-2018	09:00	1.6	E
21-Apr-2018	10:00	2.1	E
21-Apr-2018	11:00	2	SE
21-Apr-2018	12:00	2.1	ESE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

21-Apr-2018	13:00	1.7	SE
21-Apr-2018	14:00	1.2	SSE
21-Apr-2018	15:00	1.3	SSE
21-Apr-2018	16:00	1.7	ESE
21-Apr-2018	17:00	1.7	E
21-Apr-2018	18:00	0.9	ENE
21-Apr-2018	19:00	0.7	ENE
21-Apr-2018	20:00	0.6	E
21-Apr-2018	21:00	0.7	E
21-Apr-2018	22:00	0.6	E
21-Apr-2018	23:00	0.6	ENE
22-Apr-2018	00:00	0.7	ENE
22-Apr-2018	01:00	0.5	ENE
22-Apr-2018	02:00	0.6	NE
22-Apr-2018	03:00	0.5	ESE
22-Apr-2018	04:00	0.9	ESE
22-Apr-2018	05:00	0.6	SE
22-Apr-2018	06:00	0.5	SSE
22-Apr-2018	07:00	0.7	SSE
22-Apr-2018	08:00	1.1	SE
22-Apr-2018	09:00	1	SE
22-Apr-2018	10:00	1.4	N
22-Apr-2018	11:00	1.5	ENE
22-Apr-2018	12:00	2.1	NNE
22-Apr-2018	13:00	2.2	NE
22-Apr-2018	14:00	2.1	NE
22-Apr-2018	15:00	2.5	ENE
22-Apr-2018	16:00	2.6	NE
22-Apr-2018	17:00	2.2	ESE
22-Apr-2018	18:00	1.9	ESE
22-Apr-2018	19:00	1.8	SSE
22-Apr-2018	20:00	1.9	SSE
22-Apr-2018	21:00	1.5	SSE
22-Apr-2018	22:00	1.5	NE
22-Apr-2018	23:00	1.6	SE
23-Apr-2018	00:00	1.4	SSE
23-Apr-2018	01:00	1.2	SSE
23-Apr-2018	02:00	0.9	SSE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

23-Apr-2018	03:00	0.7	ESE
23-Apr-2018	04:00	1	N
23-Apr-2018	05:00	0.8	WSW
23-Apr-2018	06:00	0.9	NNW
23-Apr-2018	07:00	0.8	N
23-Apr-2018	08:00	1.6	NE
23-Apr-2018	09:00	1.7	ESE
23-Apr-2018	10:00	2.2	ENE
23-Apr-2018	11:00	2.6	SW
23-Apr-2018	12:00	2.8	N
23-Apr-2018	13:00	3.2	W
23-Apr-2018	14:00	2.6	SW
23-Apr-2018	15:00	3.2	SW
23-Apr-2018	16:00	3	SW
23-Apr-2018	17:00	2.8	WSW
23-Apr-2018	18:00	2.3	SE
23-Apr-2018	19:00	2.1	E
23-Apr-2018	20:00	2.2	NE
23-Apr-2018	21:00	2.5	NE
23-Apr-2018	22:00	2.8	ENE
23-Apr-2018	23:00	2.5	NE
24-Apr-2018	00:00	2.5	NE
24-Apr-2018	01:00	2.4	ENE
24-Apr-2018	02:00	2.5	NE
24-Apr-2018	03:00	2.1	ENE
24-Apr-2018	04:00	1.8	ENE
24-Apr-2018	05:00	2.2	ENE
24-Apr-2018	06:00	1.9	ENE
24-Apr-2018	07:00	1.9	ENE
24-Apr-2018	08:00	2.5	NE
24-Apr-2018	09:00	3.1	ENE
24-Apr-2018	10:00	3.6	ENE
24-Apr-2018	11:00	4	ENE
24-Apr-2018	12:00	3	ENE
24-Apr-2018	13:00	3.2	ENE
24-Apr-2018	14:00	2.8	ENE
24-Apr-2018	15:00	2.8	ENE
24-Apr-2018	16:00	3	ENE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

24-Apr-2018	17:00	3.3	ENE
24-Apr-2018	18:00	2.7	SW
24-Apr-2018	19:00	2.7	ENE
24-Apr-2018	20:00	2.5	ENE
24-Apr-2018	21:00	2.2	ENE
24-Apr-2018	22:00	2.8	E
24-Apr-2018	23:00	2.6	ENE
25-Apr-2018	00:00	2.9	ENE
25-Apr-2018	01:00	3.1	ENE
25-Apr-2018	02:00	2.9	ESE
25-Apr-2018	03:00	2.7	ENE
25-Apr-2018	04:00	2.6	NE
25-Apr-2018	05:00	2.5	N
25-Apr-2018	06:00	2.3	NE
25-Apr-2018	07:00	1.5	ENE
25-Apr-2018	08:00	1.6	NE
25-Apr-2018	09:00	2.6	NE
25-Apr-2018	10:00	3	ENE
25-Apr-2018	11:00	3.4	ENE
25-Apr-2018	12:00	3.1	NE
25-Apr-2018	13:00	2.7	ENE
25-Apr-2018	14:00	2.7	NE
25-Apr-2018	15:00	2.6	NE
25-Apr-2018	16:00	2.5	NE
25-Apr-2018	17:00	1.6	NNE
25-Apr-2018	18:00	1.3	ENE
25-Apr-2018	19:00	1.3	NE
25-Apr-2018	20:00	1.7	NE
25-Apr-2018	21:00	1.6	ENE
25-Apr-2018	22:00	1.5	ENE
25-Apr-2018	23:00	2.1	NE
26-Apr-2018	00:00	1.7	NE
26-Apr-2018	01:00	1.5	ENE
26-Apr-2018	02:00	1.5	ENE
26-Apr-2018	03:00	1.4	NE
26-Apr-2018	04:00	1.6	E
26-Apr-2018	05:00	1.1	ENE
26-Apr-2018	06:00	0.6	ENE

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

26-Apr-2018	07:00	0.8	ENE
26-Apr-2018	08:00	0.7	ENE
26-Apr-2018	09:00	1.7	SSE
26-Apr-2018	10:00	2	SSE
26-Apr-2018	11:00	2	SSE
26-Apr-2018	12:00	2.8	SE
26-Apr-2018	13:00	3	SSE
26-Apr-2018	14:00	2.7	SSE
26-Apr-2018	15:00	2.4	SSE
26-Apr-2018	16:00	2.2	SSE
26-Apr-2018	17:00	1.8	SSE
26-Apr-2018	18:00	1.3	ENE
26-Apr-2018	19:00	1.1	ENE
26-Apr-2018	20:00	0.8	E
26-Apr-2018	21:00	0.6	E
26-Apr-2018	22:00	0.4	E
26-Apr-2018	23:00	0.7	E
27-Apr-2018	00:00	0.9	NNE
27-Apr-2018	01:00	0.9	ENE
27-Apr-2018	02:00	0.9	ENE
27-Apr-2018	03:00	1.7	NNE
27-Apr-2018	04:00	1.5	NNE
27-Apr-2018	05:00	1.9	NNE
27-Apr-2018	06:00	1.7	ENE
27-Apr-2018	07:00	2	NE
27-Apr-2018	08:00	2.2	N
27-Apr-2018	09:00	2.4	W
27-Apr-2018	10:00	2.7	N
27-Apr-2018	11:00	3.4	ENE
27-Apr-2018	12:00	2.9	ENE
27-Apr-2018	13:00	2.9	ENE
27-Apr-2018	14:00	3.1	NNE
27-Apr-2018	15:00	2.7	ESE
27-Apr-2018	16:00	2.5	SSE
27-Apr-2018	17:00	2.6	ESE
27-Apr-2018	18:00	2	ESE
27-Apr-2018	19:00	2	E
27-Apr-2018	20:00	2.5	E

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

27-Apr-2018	21:00	3.2	E
27-Apr-2018	22:00	1.6	ESE
27-Apr-2018	23:00	1.8	E
28-Apr-2018	00:00	1.8	ENE
28-Apr-2018	01:00	1.9	ENE
28-Apr-2018	02:00	2.1	E
28-Apr-2018	03:00	1.8	E
28-Apr-2018	04:00	1.7	E
28-Apr-2018	05:00	1.5	ENE
28-Apr-2018	06:00	1.5	ENE
28-Apr-2018	07:00	1.6	NE
28-Apr-2018	08:00	2.1	ENE
28-Apr-2018	09:00	2.6	NE
28-Apr-2018	10:00	3.1	ENE
28-Apr-2018	11:00	3.4	ENE
28-Apr-2018	12:00	3.2	ENE
28-Apr-2018	13:00	3	NNE
28-Apr-2018	14:00	2.6	NNE
28-Apr-2018	15:00	2.3	NNE
28-Apr-2018	16:00	2.4	ENE
28-Apr-2018	17:00	2.2	ENE
28-Apr-2018	18:00	1.8	E
28-Apr-2018	19:00	1.7	ENE
28-Apr-2018	20:00	1.5	NE
28-Apr-2018	21:00	2	ENE
28-Apr-2018	22:00	1.7	NE
28-Apr-2018	23:00	1.6	ENE
29-Apr-2018	00:00	1.5	ENE
29-Apr-2018	01:00	1.4	ENE
29-Apr-2018	02:00	1.4	ENE
29-Apr-2018	03:00	1.2	ENE
29-Apr-2018	04:00	1.3	ENE
29-Apr-2018	05:00	1.3	ENE
29-Apr-2018	06:00	1.1	E
29-Apr-2018	07:00	1.3	E
29-Apr-2018	08:00	1.5	E
29-Apr-2018	09:00	2	E
29-Apr-2018	10:00	2.7	E

**APPENDIX C –
WEATHER CONDITIONS DURING THE MONITORING PERIOD**

II. Mean Wind Speed and Wind Direction

29-Apr-2018	11:00	2.7	NNE
29-Apr-2018	12:00	2.2	ENE
29-Apr-2018	13:00	2	ENE
29-Apr-2018	14:00	1.8	ENE
29-Apr-2018	15:00	2	ENE
29-Apr-2018	16:00	1.5	ENE
29-Apr-2018	17:00	1.5	NE
29-Apr-2018	18:00	1.1	NE
29-Apr-2018	19:00	0.5	NE
29-Apr-2018	20:00	0.6	NE
29-Apr-2018	21:00	0.7	ENE
29-Apr-2018	22:00	0.9	NE
29-Apr-2018	23:00	0.7	ENE
30-Apr-2018	00:00	0.7	NE
30-Apr-2018	01:00	0.8	NE
30-Apr-2018	02:00	0.7	NE
30-Apr-2018	03:00	0.7	NE
30-Apr-2018	04:00	1.1	ENE
30-Apr-2018	05:00	0.9	ENE
30-Apr-2018	06:00	1	ENE
30-Apr-2018	07:00	1.7	ENE
30-Apr-2018	08:00	2	ENE
30-Apr-2018	09:00	2.1	ENE
30-Apr-2018	10:00	2.2	ENE
30-Apr-2018	11:00	2.2	ENE
30-Apr-2018	12:00	2.7	ENE
30-Apr-2018	13:00	2.7	ENE
30-Apr-2018	14:00	2.2	NE
30-Apr-2018	15:00	2.3	E
30-Apr-2018	16:00	1.8	ENE
30-Apr-2018	17:00	2	ESE
30-Apr-2018	18:00	1.6	ENE
30-Apr-2018	19:00	1.6	NE
30-Apr-2018	20:00	1.3	ESE
30-Apr-2018	21:00	1.2	ENE
30-Apr-2018	22:00	1.2	NE
30-Apr-2018	23:00	1.1	ENE

**APPENDIX D
ENVIRONMENTAL MONITORING
SCHEDULES**

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Impact Air Quality and Noise Monitoring Schedule (April 2018)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Apr	2-Apr	3-Apr	4-Apr	5-Apr	6-Apr	7-Apr
		1 hr TSP X3 [AM1, AM2, AM3, AM4] [AM5(A), AM6(A)] Noise [CM1, CM2, CM4] [CM6(A), CM7(A), CM8(A)]	24 hr TSP		Noise [CM3, CM5]	
8-Apr	9-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr
	1 hr TSP X3 [AM1, AM2, AM3, AM4] [AM5(A), AM6(A)]	24 hr TSP	1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4] [CM3, CM5]		1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)]	
15-Apr	16-Apr	17-Apr	18-Apr	19-Apr	20-Apr	21-Apr
	24 hr TSP	1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4]	Noise [CM3, CM5]	1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)]	24 hr TSP	
22-Apr	23-Apr	24-Apr	25-Apr	26-Apr	27-Apr	28-Apr
	1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4]	Noise [CM3, CM5]	1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)]	24 hr TSP	1 hr TSP X3 [AM1, AM2, AM3, AM4]	
29-Apr	30-Apr					
	1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)]					

Air Quality Monitoring Station

AM1 - Tin Hau Temple
AM2 - Sai Tso Wan Recreation Ground
AM3 - Yau Lai Estate Bik Lai House
AM4⁽¹⁾ - Sitting-out Area at Cha Kwo Ling Village
AM4(A)⁽²⁾ - Cha Kwo Ling Public Cargo Working Area Administrative Office
AM5(A) - Tseung Kwan O DSD Desilting Compound
AM6(A) - Park Central, L1/F Open Space Area

Noise Monitoring Station

CM1 - Nga Lai House, Yau Lai Estate Phase 1, Yau Tong
CM2 - Bik Lai House, Yau Lai Estate Phase 1, Yau Tong
CM3 - Block S, Yau Lai Estate Phase 5, Yau Tong
CM4 - Tin Hau Temple, Cha Kwo Ling
CM5 - CCC Kei Faat Primary School, Yau Tong
CM6(A) - Site Boundary of Contract No. NE/2015/02 near Tower 1, Ocean Shores
CM7(A) - Site Boundary of Contract No. NE/2015/02 near Tower 7, Ocean Shores
CM8(A) - Park Central, L1/F Open Space Area

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Impact Water Quality Monitoring Schedule (April 2018)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Apr	2-Apr	3-Apr	4-Apr	5-Apr	6-Apr	7-Apr
			Mid-Flood 08:25 Mid-Ebb 14:45		Mid-Flood 09:19 Mid-Ebb 16:06	
8-Apr	9-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr
		Mid-Flood 13:17 Mid-Ebb 20:43		Mid-Ebb 10:37 Mid-Flood 15:37		Mid-Ebb 11:38 Mid-Flood 17:23
15-Apr	16-Apr	17-Apr	18-Apr	19-Apr	20-Apr	21-Apr
	Mid-Ebb 12:42 Mid-Flood 18:56		Mid-Flood 07:33 Mid-Ebb 13:58		Mid-Flood 08:42 Mid-Ebb 15:28	
22-Apr	23-Apr	24-Apr	25-Apr	26-Apr	27-Apr	28-Apr
	Mid-Flood 11:21 Mid-Ebb 18:57		Mid-Ebb 09:13 Mid-Flood 14:34		Mid-Ebb 10:49 Mid-Flood 16:43	
29-Apr	30-Apr					
	Mid-Ebb 12:35 Mid-Flood 19:05					

Note: No marine construction works under this Project from 30 March 2018 to 2 April 2018.

Monitoring Station:

C1, C2, G1, G2, G3, G4, M1, M2, M3, M4, M5, M6

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Impact Groundwater Quality Monitoring Schedule (April 2018)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Apr	2-Apr	3-Apr	4-Apr	5-Apr	6-Apr	7-Apr
8-Apr	9-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr
			Groundwater Quality Monitoring			
15-Apr	16-Apr	17-Apr	18-Apr	19-Apr	20-Apr	21-Apr
22-Apr	23-Apr	24-Apr	25-Apr	26-Apr	27-Apr	28-Apr
		Groundwater Quality Monitoring				
29-Apr	30-Apr					

Monitoring Location:

Stream 1, Stream 2, Stream 3

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Impact Water Quality Monitoring Schedule in Temporary Marine Embayment (April 2018)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Apr	2-Apr	3-Apr	4-Apr	5-Apr	6-Apr	7-Apr
					Mid-Flood 09:19 Mid-Ebb 16:06	
8-Apr	9-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr
			Mid-Ebb 09:57 Mid-Flood 14:35			
15-Apr	16-Apr	17-Apr	18-Apr	19-Apr	20-Apr	21-Apr
				Mid-Flood 08:07 Mid-Ebb 14:41		
22-Apr	23-Apr	24-Apr	25-Apr	26-Apr	27-Apr	28-Apr
		Mid-Ebb 07:50 Mid-Flood 12:54				
29-Apr	30-Apr					

Monitoring Station:
W1

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Tentative Impact Air Quality and Noise Monitoring Schedule (May 2018)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-May	2-May	3-May	4-May	5-May
			24 hr TSP	1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4] [CM3, CM5]	1 hr TSP X3 [AM5(A), AM6(A)]	
6-May	7-May	8-May	9-May	10-May	11-May	12-May
	24 hr TSP	1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4]		1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)]	24 hr TSP Noise [CM3, CM5]	
13-May	14-May	15-May	16-May	17-May	18-May	19-May
	1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4]	1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)] [CM3, CM5]		24 hr TSP	1 hr TSP X3 [AM1, AM2, AM3, AM4]	
20-May	21-May	22-May	23-May	24-May	25-May	26-May
	1 hr TSP X3 [AM5(A), AM6(A)]		24 hr TSP	1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4] [CM3, CM5]	1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)]	
27-May	28-May	29-May	30-May	31-May		
	Noise [CM3, CM5]	24 hr TSP	1 hr TSP X3 [AM1, AM2, AM3, AM4] Noise [CM1, CM2, CM4]	1 hr TSP X3 [AM5(A), AM6(A)] Noise [CM6(A), CM7(A), CM8(A)]		

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Air Quality Monitoring Station

AM1 - Tin Hau Temple
AM2 - Sai Tso Wan Recreation Ground
AM3 - Yau Lai Estate Bik Lai House
AM4⁽¹⁾ - Sitting-out Area at Cha Kwo Ling Village
AM4(A)⁽²⁾ - Cha Kwo Ling Public Cargo Working Area Administrative Office
AM5(A) - Tseung Kwan O DSD Desilting Compound
AM6(A) - Park Central, L1/F Open Space Area

Noise Monitoring Station

CM1 - Nga Lai House, Yau Lai Estate Phase 1, Yau Tong
CM2 - Bik Lai House, Yau Lai Estate Phase 1, Yau Tong
CM3 - Block S, Yau Lai Estate Phase 5, Yau Tong
CM4 - Tin Hau Temple, Cha Kwo Ling
CM5 - CCC Kei Faat Primary School, Yau Tong
CM6(A) - Site Boundary of Contract No. NE/2015/02 near Tower 1, Ocean Shores
CM7(A) - Site Boundary of Contract No. NE/2015/02 near Tower 7, Ocean Shores
CM8(A) - Park Central, L1/F Open Space Area

Note (1) For 1-hour TSP monitoring; (2) For 24-hour TSP monitoring

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Tentative Impact Water Quality Monitoring Schedule (May 2018)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-May	2-May	3-May	4-May	5-May
			Mid-Flood 07:16 Mid-Ebb 13:44		Mid-Flood 08:10 Mid-Ebb 14:56	
6-May	7-May	8-May	9-May	10-May	11-May	12-May
	Mid-Flood# 04:40 Mid-Ebb 17:15		Mid-Flood 12:39 Mid-Ebb 19:34		Mid-Ebb 10:01 Mid-Flood 15:10	
13-May	14-May	15-May	16-May	17-May	18-May	19-May
	Mid-Ebb 11:39 Mid-Flood 17:57		Mid-Ebb 12:58 Mid-Flood 19:34		Mid-Flood 07:39 Mid-Ebb 14:28	
20-May	21-May	22-May	23-May	24-May	25-May	26-May
	Mid-Flood 10:02 Mid-Ebb 17:24		Mid-Flood 12:52 Mid-Ebb 19:48		Mid-Ebb 09:43 Mid-Flood 15:38	
27-May	28-May	29-May	30-May	31-May		
	Mid-Ebb 11:41 Mid-Flood 18:17		Mid-Ebb 12:50 Mid-Flood 19:46			

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Monitoring Station:

C1, C2, G1, G2, G3, G4, M1, M2, M3, M4, M5, M6

Remark(#): It is proposed that there is no need for mid-flood monitoring on 7 May 2018 based on the following reasons:

- a) There will be no marine works within the suitable tidal conditions (within ± 1.5 hour of the predicted mid-ebb or mid-flood tides).
- b) The above condition described in point a) occur for 2 or more consecutive days.

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Tentative Impact Groundwater Quality Monitoring Schedule (May 2018)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-May	2-May	3-May	4-May	5-May
6-May	7-May	8-May	9-May	10-May	11-May	12-May
					Groundwater Quality Monitoring	
13-May	14-May	15-May	16-May	17-May	18-May	19-May
20-May	21-May	22-May	23-May	24-May	25-May	26-May
				Groundwater Quality Monitoring		
27-May	28-May					

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Monitoring Location:

Stream 1, Stream 2, Stream 3

Agreement No. CE/59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction
Tentative Impact Water Quality Monitoring Schedule in Temporary Marine Embayment (May 2018)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-May	2-May	3-May	4-May	5-May
				Mid-Flood 07:44 Mid-Ebb 14:20		
6-May	7-May	8-May	9-May	10-May	11-May	12-May
					Mid-Ebb 10:01 Mid-Flood 15:10	
13-May	14-May	15-May	16-May	17-May	18-May	19-May
		Mid-Ebb 12:17 Mid-Flood 18:46				
20-May	21-May	22-May	23-May	24-May	25-May	26-May
				Mid-Ebb 08:47 Mid-Flood 14:27		
27-May	28-May	29-May	30-May	31-May		
	Mid-Ebb 11:41 Mid-Flood 18:17					

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

Monitoring Station:

W1

**APPENDIX E
1-HOUR TSP MONITORING RESULTS
AND GRAPHICAL PRESENTATIONS**

Appendix E - 1-hour TSP Monitoring Results

Location AM1 - Tin Hau Temple			
Date	Time	Weather	Particulate Concentration ($\mu\text{g}/\text{m}^3$)
3-Apr-18	13:00	Sunny	271.8
3-Apr-18	14:00	Sunny	258.9
3-Apr-18	15:00	Sunny	248.4
9-Apr-18	13:00	Sunny	268.7
9-Apr-18	14:00	Sunny	264.3
9-Apr-18	15:00	Sunny	264.1
11-Apr-18	13:00	Cloudy	191.8
11-Apr-18	14:00	Cloudy	176.5
11-Apr-18	15:00	Cloudy	201.0
17-Apr-18	9:00	Cloudy	174.4
17-Apr-18	10:00	Cloudy	193.0
17-Apr-18	11:00	Cloudy	184.9
23-Apr-18	9:00	Sunny	152.2
23-Apr-18	10:00	Sunny	156.0
23-Apr-18	11:00	Sunny	156.9
27-Apr-18	9:00	Sunny	179.5
27-Apr-18	10:00	Sunny	198.3
27-Apr-18	11:00	Sunny	207.3
		Average	208.2
		Maximum	271.8
		Minimum	152.2

Location AM2 - Sai Tso Wan Recreation Ground			
Date	Time	Weather	Particulate Concentration ($\mu\text{g}/\text{m}^3$)
3-Apr-18	9:00	Sunny	237.3
3-Apr-18	10:00	Sunny	261.5
3-Apr-18	11:00	Sunny	249.7
9-Apr-18	9:00	Sunny	242.5
9-Apr-18	10:00	Sunny	246.1
9-Apr-18	11:00	Sunny	248.4
11-Apr-18	13:00	Sunny	198.2
11-Apr-18	14:00	Sunny	190.2
11-Apr-18	15:00	Sunny	213.9
17-Apr-18	9:00	Cloudy	162.3
17-Apr-18	10:00	Cloudy	176.7
17-Apr-18	11:00	Cloudy	164.2
23-Apr-18	9:00	Sunny	131.6
23-Apr-18	10:00	Sunny	148.4
23-Apr-18	11:00	Sunny	128.0
27-Apr-18	9:00	Sunny	161.7
27-Apr-18	10:00	Sunny	164.2
27-Apr-18	11:00	Sunny	178.1
		Average	194.6
		Maximum	261.5
		Minimum	128.0

Appendix E - 1-hour TSP Monitoring Results

Location AM3 - Yau Lai Estate Bik Lai House			
Date	Time	Weather	Particulate Concentration ($\mu\text{g}/\text{m}^3$)
3-Apr-18	9:00	Sunny	176.4
3-Apr-18	10:00	Sunny	175.7
3-Apr-18	11:00	Sunny	185.9
9-Apr-18	9:00	Sunny	266.7
9-Apr-18	10:00	Sunny	270.1
9-Apr-18	11:00	Sunny	267.9
11-Apr-18	9:00	Cloudy	249.1
11-Apr-18	10:00	Cloudy	254.9
11-Apr-18	11:00	Cloudy	251.0
17-Apr-18	13:00	Cloudy	191.9
17-Apr-18	14:00	Cloudy	184.4
17-Apr-18	15:00	Cloudy	195.5
23-Apr-18	13:00	Sunny	209.8
23-Apr-18	14:00	Sunny	203.3
23-Apr-18	15:00	Sunny	198.5
27-Apr-18	13:00	Sunny	233.3
27-Apr-18	14:00	Sunny	241.7
27-Apr-18	15:00	Sunny	247.7
Average			222.4
Maximum			270.1
Minimum			175.7




Location AM4 - Sitting-out Area at Cha Kwo Ling Village			
Date	Time	Weather	Particulate Concentration ($\mu\text{g}/\text{m}^3$)
3-Apr-18	13:00	Sunny	264.5
3-Apr-18	14:00	Sunny	254.9
3-Apr-18	15:00	Sunny	268.4
9-Apr-18	13:00	Sunny	256.2
9-Apr-18	14:00	Sunny	259.1
9-Apr-18	15:00	Sunny	262.1
11-Apr-18	9:00	Sunny	235.7
11-Apr-18	10:00	Sunny	213.2
11-Apr-18	11:00	Sunny	222.8
17-Apr-18	13:00	Cloudy	162.5
17-Apr-18	14:00	Cloudy	164.7
17-Apr-18	15:00	Cloudy	161.0
23-Apr-18	13:00	Sunny	195.3
23-Apr-18	14:00	Sunny	203.5
23-Apr-18	15:00	Sunny	206.3
27-Apr-18	13:00	Sunny	222.1
27-Apr-18	14:00	Sunny	216.0
27-Apr-18	15:00	Sunny	220.3
Average			221.6
Maximum			268.4
Minimum			161.0

Appendix E - 1-hour TSP Monitoring Results

Location AM5(A) - Tseung Kwan O DSD Desilting Compound			
Date	Time	Weather	Particulate Concentration ($\mu\text{g}/\text{m}^3$)
3-Apr-18	9:00	Sunny	22.1
3-Apr-18	10:00	Sunny	24.4
3-Apr-18	11:00	Sunny	26.8
9-Apr-18	13:00	Sunny	17.5
9-Apr-18	14:00	Sunny	16.3
9-Apr-18	15:00	Sunny	15.1
13-Apr-18	13:00	Sunny	207.4
13-Apr-18	14:00	Sunny	233.4
13-Apr-18	15:00	Sunny	225.5
19-Apr-18	8:50	Sunny	28.7
19-Apr-18	9:50	Sunny	27.6
19-Apr-18	10:50	Sunny	25.4
25-Apr-18	13:00	Cloudy	133.9
25-Apr-18	14:00	Cloudy	139.5
25-Apr-18	15:00	Cloudy	146.3
30-Apr-18	9:00	Cloudy	250.9
30-Apr-18	10:00	Cloudy	238.9
30-Apr-18	11:00	Cloudy	244.3
		Average	112.4
		Maximum	250.9
		Minimum	15.1

Location AM6(A) - Park Central, L1/F Open Space Area			
Date	Time	Weather	Particulate Concentration ($\mu\text{g}/\text{m}^3$)
3-Apr-18	13:15	Sunny	19.8
3-Apr-18	14:15	Sunny	17.5
3-Apr-18	15:15	Sunny	19.8
9-Apr-18	9:00	Sunny	14.0
9-Apr-18	10:00	Sunny	14.0
9-Apr-18	11:00	Sunny	12.8
13-Apr-18	9:00	Sunny	187.3
13-Apr-18	10:00	Sunny	200.0
13-Apr-18	11:00	Sunny	198.6
19-Apr-18	13:00	Sunny	33.1
19-Apr-18	14:00	Sunny	33.1
19-Apr-18	15:00	Sunny	28.7
25-Apr-18	8:30	Cloudy	113.4
25-Apr-18	9:30	Cloudy	115.7
25-Apr-18	10:30	Cloudy	118.0
30-Apr-18	13:00	Cloudy	250.6
30-Apr-18	14:00	Cloudy	240.9
30-Apr-18	15:00	Cloudy	256.5
		Average	104.1
		Maximum	256.5
		Minimum	12.8

1-hr TSP Concentration Levels

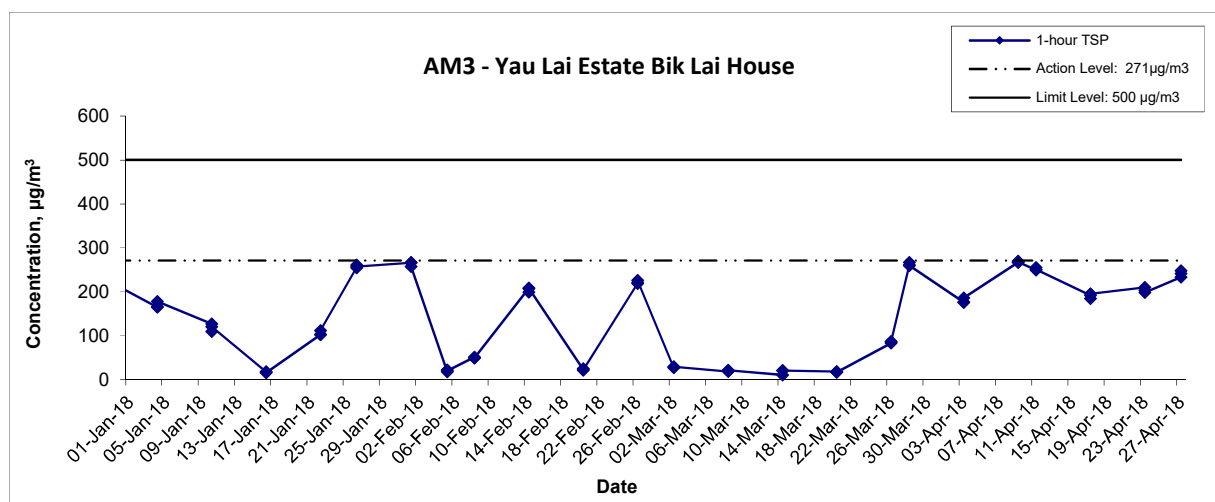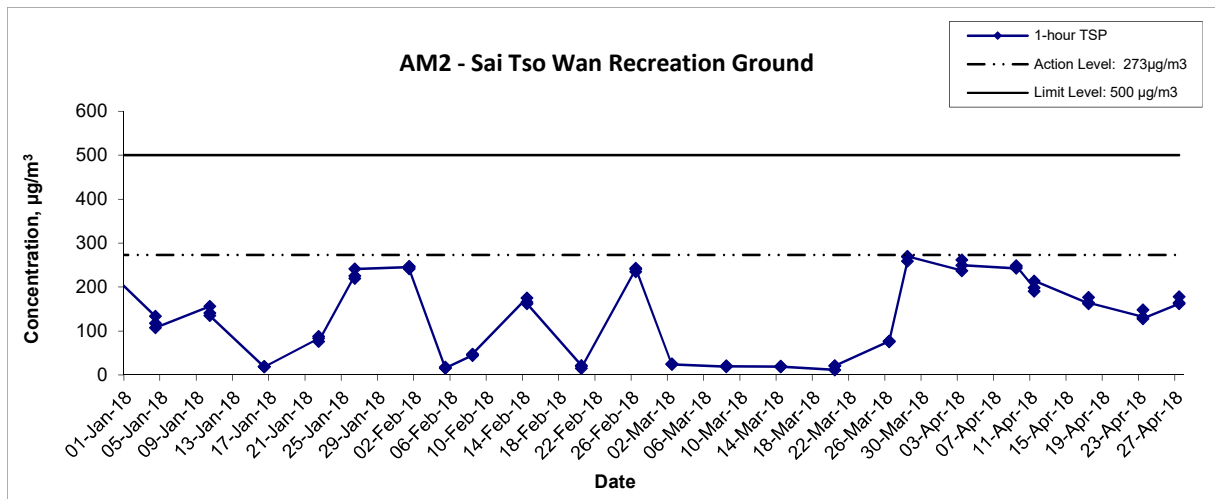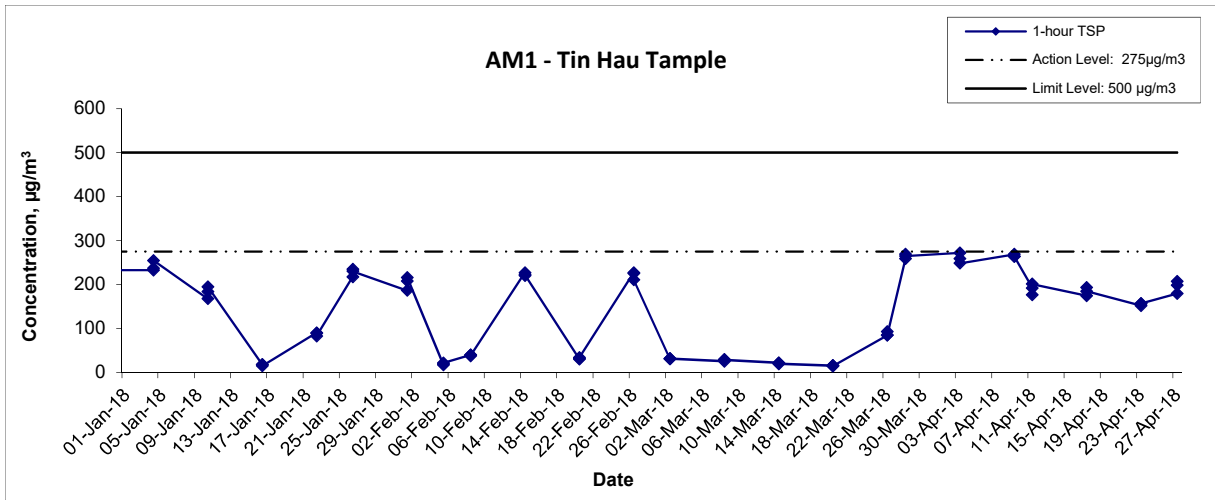

Title Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel -
 Design and Construction

Graphical Presentation of 1-hour TSP Monitoring Results

Scale N.T.S




Date Apr 18

Project No. MA16034

Appendix E



1-hr TSP Concentration Levels

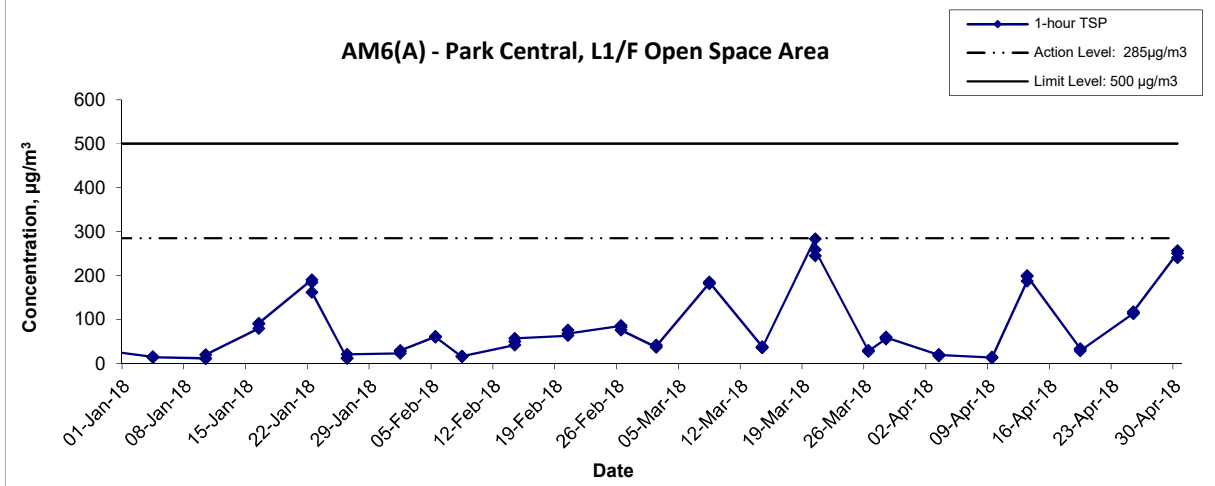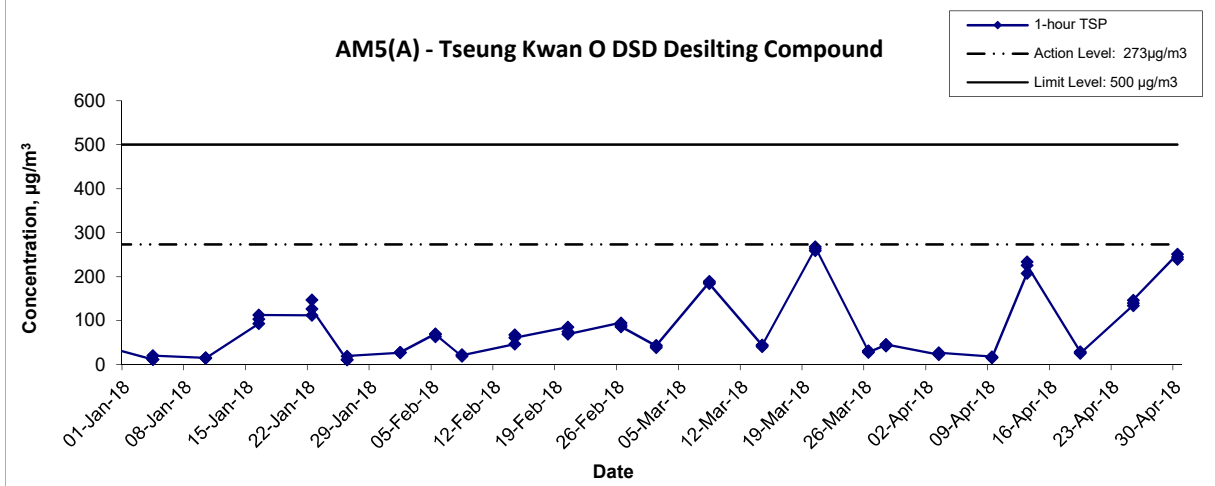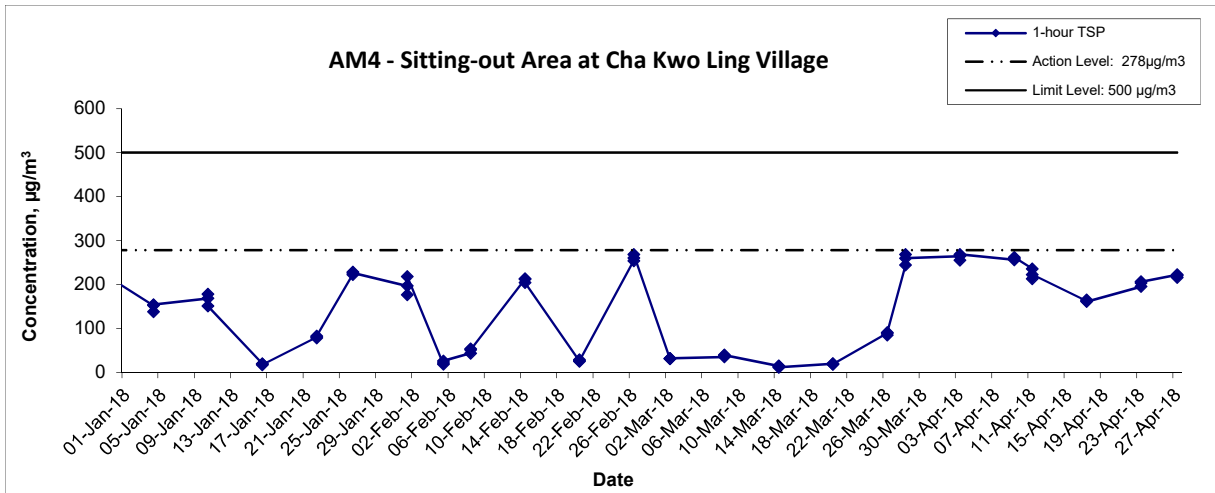

Title Agreement No. CE/59/2015 (EP)
 Environmental Team for Tseung Kwan O - Lam Tin Tunnel -
 Design and Construction
 Graphical Presentation of 1-hour TSP Monitoring Results

Scale N.T.S
 Project No. MA16034
 Date Apr 18
 Appendix E



**APPENDIX F
24-HOUR TSP MONITORING RESULTS
AND GRAPHICAL PRESENTATIONS**

Appendix F - 24-hour TSP Monitoring Results

Location AM1 - Tin Hau Temple

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate Weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Conc. (µg/m ³)
				Initial	Final		Initial	Final		Initial	Final			
4-Apr-18	Sunny	298.1	762.8	2.8218	3.0619	0.2401	3323.0	3347.0	24.0	1.22	1.22	1.22	1752.4	137.0
10-Apr-18	Cloudy	296.2	764.4	2.8608	3.0939	0.2331	3347.0	3371.0	24.0	1.22	1.22	1.22	1760.8	132.4
16-Apr-18	Cloudy	289.0	765.2	2.8658	2.9887	0.1229	3371.0	3395.0	24.0	1.24	1.24	1.24	1786.4	68.8
20-Apr-18	Cloudy	295.3	763.1	3.6315	3.8912	0.2597	3395.0	3419.0	24.0	1.22	1.22	1.22	1762.1	147.4
26-Apr-18	Cloudy	296.2	762.8	3.3734	3.5290	0.1556	3419.0	3443.0	24.0	1.22	1.22	1.22	1758.7	88.5
													Min	68.8
													Max	147.4
													Average	114.8

Location AM2 - Sai Tso Wan Recreation Ground

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate Weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Conc. (µg/m ³)
				Initial	Final		Initial	Final		Initial	Final			
4-Apr-18	Sunny	298.4	762.4	2.8285	2.9548	0.1263	24287.3	24311.3	24.0	1.22	1.21	1.21	1749.3	72.2
10-Apr-18	Sunny	296.8	764.7	2.8965	2.9852	0.0887	24311.3	24335.3	24.0	1.22	1.22	1.22	1757.2	50.5
16-Apr-18	Cloudy	288.5	765.8	2.8605	2.9259	0.0654	24335.3	24359.3	24.0	1.24	1.24	1.24	1785.7	36.6
20-Apr-18	Cloudy	295.8	763.7	3.3428	3.4305	0.0877	24359.3	24383.3	24.0	1.22	1.22	1.22	1759.2	49.9
26-Apr-18	Cloudy	296.4	762.7	3.3650	3.5076	0.1426	24383.3	24407.3	24.0	1.22	1.22	1.22	1756.0	81.2
													Min	36.6
													Max	81.2
													Average	58.1

Location AM3 - Yau Lai Estate, Bik Lai House

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate Weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Conc. (µg/m ³)
				Initial	Final		Initial	Final		Initial	Final			
4-Apr-18	Sunny	298.0	763.3	2.8710	3.0152	0.1442	12854.7	12878.7	24.0	1.22	1.22	1.22	1754.2	82.2
10-Apr-18	Cloudy	296.7	764.1	3.2805	3.4294	0.1489	12878.7	12902.7	24.0	1.22	1.22	1.22	1759.2	84.6
16-Apr-18	Cloudy	288.2	765.6	2.8274	2.8814	0.0540	12902.7	12926.7	24.0	1.24	1.24	1.24	1788.1	30.2
20-Apr-18	Cloudy	296.4	763.2	3.3494	3.4507	0.1013	12926.7	12950.7	24.0	1.22	1.22	1.22	1759.0	57.6
26-Apr-18	Cloudy	296.6	762.3	3.3485	3.4410	0.0925	12950.7	12974.7	24.0	1.22	1.22	1.22	1757.3	52.6
													Min	30.2
													Max	84.6
													Average	61.5

Appendix F - 24-hour TSP Monitoring Results

Location AM4(A) - Cha Kwo Ling Public Cargo Working Area Administrative Office

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate Weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Conc. (µg/m ³)
				Initial	Final		Initial	Final		Initial	Final			
4-Apr-18	Sunny	298.8	762.5	2.8810	3.2366	0.3556	9841.2	9865.2	24.0	1.21	1.21	1.21	1737.8	204.6
10-Apr-18	Sunny	296.7	764.4	2.9001	3.2497	0.3496	9865.2	9889.2	24.0	1.21	1.21	1.21	1746.5	200.2
16-Apr-18	Cloudy	288.4	766.0	2.8331	3.0564	0.2233	9889.2	9913.2	24.0	1.23	1.23	1.23	1774.5	125.8
20-Apr-18	Cloudy	295.0	764.7	3.6375	3.9309	0.2934	9913.2	9937.2	24.0	1.22	1.22	1.22	1752.1	167.5
26-Apr-18	Cloudy	295.7	762.6	3.3488	3.6560	0.3072	9937.2	9961.2	24.0	1.21	1.21	1.21	1747.4	175.8
													Min	125.8
													Max	204.6
													Average	174.8




Location AM5(A) - Tseung Kwan O DSD Desilting Compound

Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate Weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Conc. (µg/m ³)
				Initial	Final		Initial	Final		Initial	Final			
4-Apr-18	Sunny	298.1	762.9	2.8531	2.9990	0.1459	26170.9	26194.9	24.0	1.21	1.21	1.21	1736.1	84.0
10-Apr-18	Sunny	297.0	764.6	2.8323	2.9600	0.1277	26194.9	26218.9	24.0	1.21	1.21	1.21	1741.7	73.3
16-Apr-18	Sunny	289.4	764.8	3.6058	3.7022	0.0964	26218.9	26242.9	24.0	1.23	1.23	1.23	1766.6	54.6
20-Apr-18	Cloudy	295.2	763.6	3.2478	3.3674	0.1196	26242.9	26266.9	24.0	1.21	1.21	1.21	1746.2	68.5
26-Apr-18	Cloudy	296.3	762.4	3.3558	3.4605	0.1047	26266.9	26290.9	24.0	1.21	1.21	1.21	1741.2	60.1
													Min	54.6
													Max	84.0
													Average	68.1

Location AM6(A) - Park Central, L1/F Open Space Area




Start Date	Weather Condition	Air Temp. (K)	Atmospheric Pressure, Pa (mmHg)	Filter Weight (g)		Particulate Weight (g)	Elapse Time		Sampling Time(hrs.)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Conc. (µg/m ³)
				Initial	Final		Initial	Final		Initial	Final			
4-Apr-18	Sunny	298.4	764.3	3.3906	3.5106	0.1200	16643.8	16667.8	24.0	1.22	1.22	1.22	1753.4	68.4
10-Apr-18	Sunny	296.0	764.9	3.6572	3.7928	0.1356	16667.8	16691.8	24.0	1.22	1.22	1.22	1761.2	77.0
16-Apr-18	Sunny	288.8	765.1	3.6196	3.6927	0.0731	16691.8	16715.8	24.0	1.24	1.24	1.24	1783.4	41.0
20-Apr-18	Cloudy	296.5	763.6	3.6470	3.8386	0.1916	16715.8	16739.8	24.0	1.22	1.22	1.22	1758.2	109.0
26-Apr-18	Cloudy	296.6	762.7	3.3618	3.4988	0.1370	16739.8	16763.8	24.0	1.22	1.22	1.22	1756.9	78.0
													Min	41.0
													Max	109.0
													Average	74.7

24-hr TSP Concentration Levels

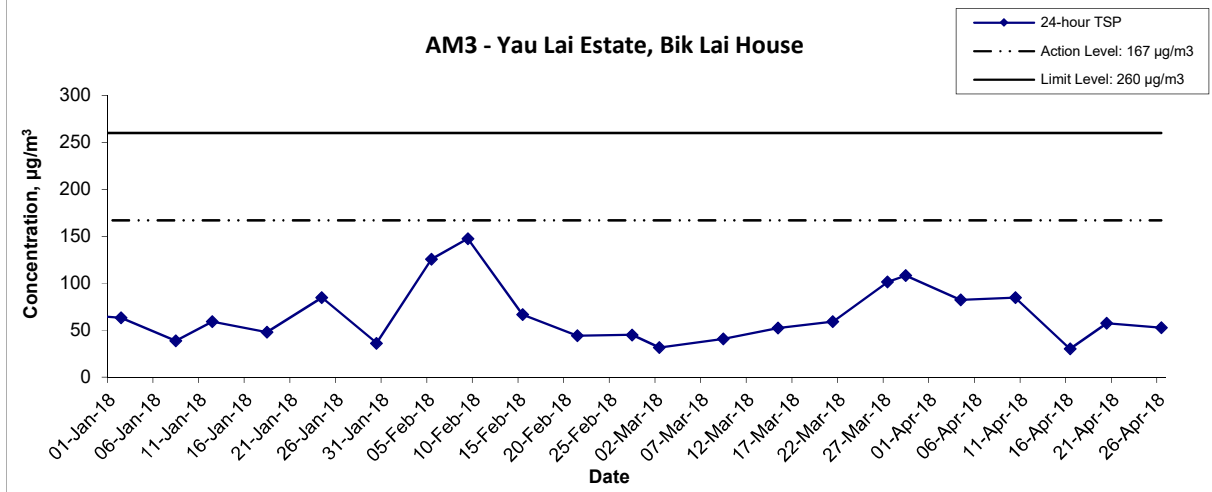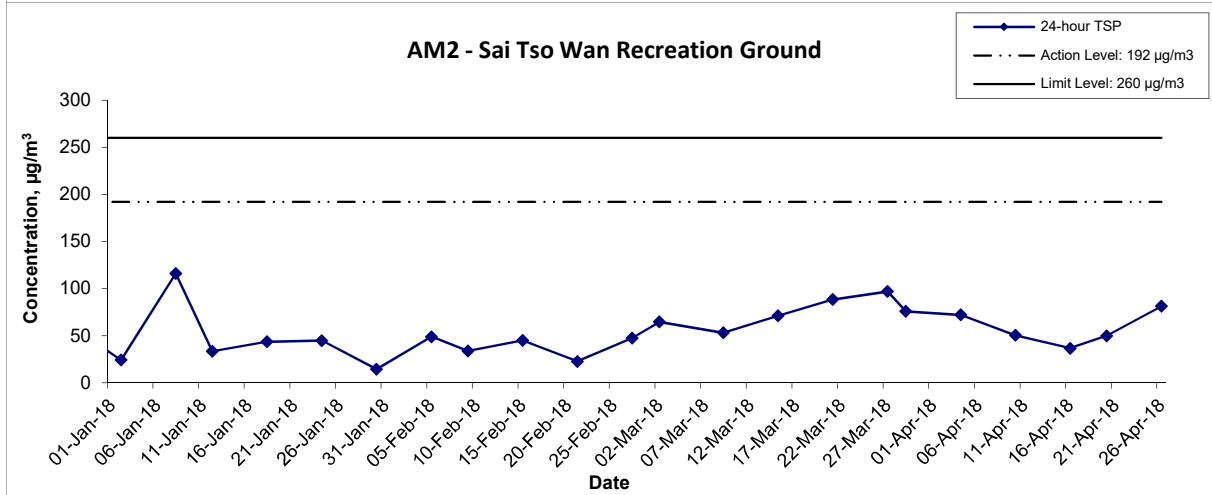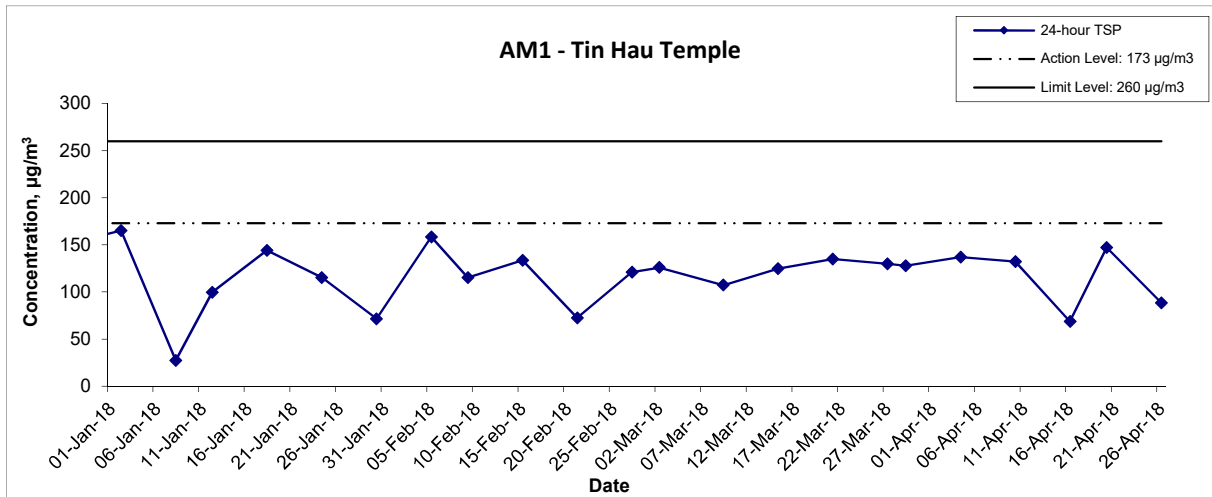

Title	Agreement No. CE/59/2015 (EP)	Scale	N.T.S	Project No.	MA16034	CINOTECH
	Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction	Date	Apr 18	Appendix	F	
Graphical Presentation of 24-hour TSP Monitoring Results						

24-hr TSP Concentration Levels

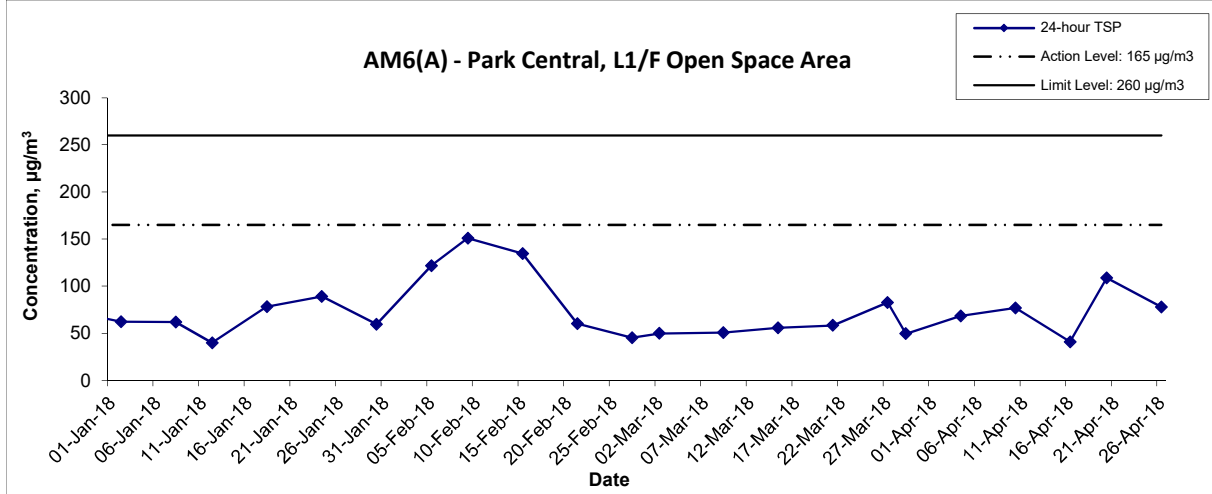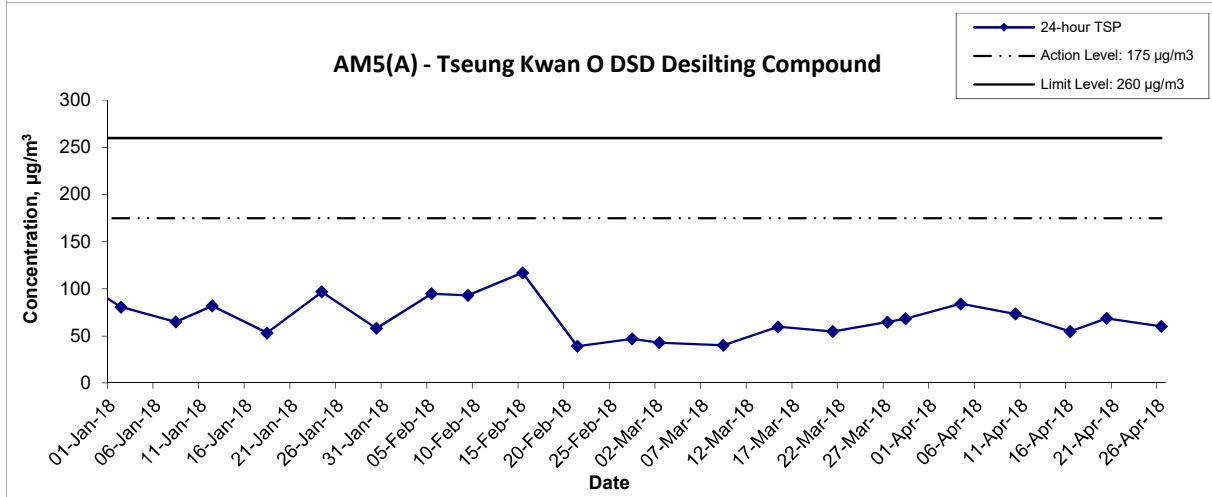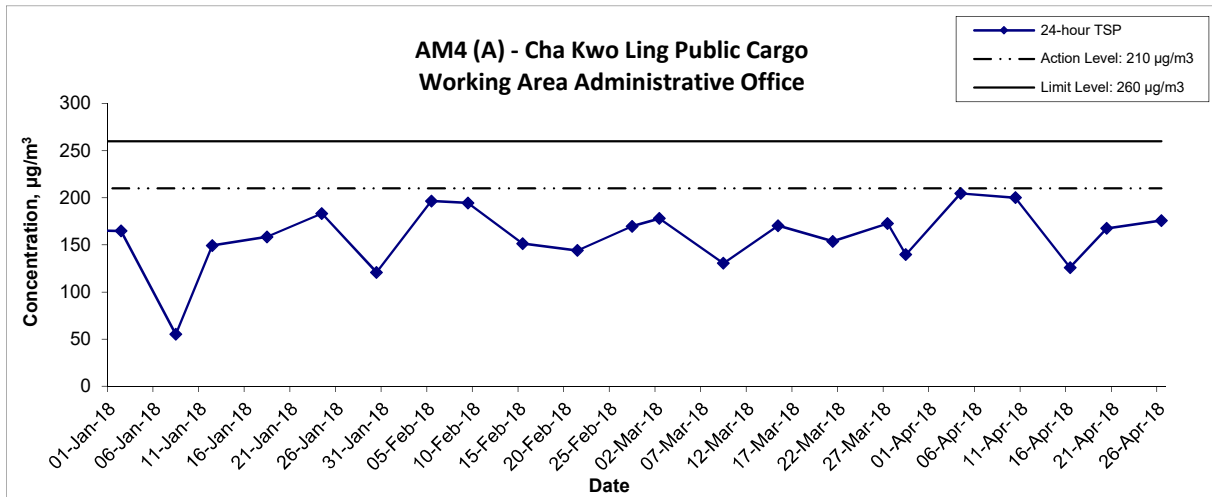

Title	Agreement No. CE/59/2015 (EP)	Scale	N.T.S	Project No.	MA16034	CINOTECH
	Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction	Date	Apr 18	Appendix	F	
Graphical Presentation of 24-hour TSP Monitoring Results						

**APPENDIX G
NOISE MONITORING RESULTS AND
GRAPHICAL PRESENTATIONS**

Appendix G - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Location CM1 - Nga Lai House, Yau Lai Estate Phase 1, Yau Tong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
3-Apr-18	10:30	Sunny	69.0	70.9	66.3	65.5	66.4
11-Apr-18	11:30	Cloudy	71.2	73.9	72.1		69.8
17-Apr-18	13:40	Cloudy	69.8	72.2	67.1		67.8
23-Apr-18	14:15	Sunny	74.2	76.5	72.1		73.6

Location CM2 - Bik Lai House, Yau Lai Estate Phase 1, Yau Tong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
3-Apr-18	09:30	Sunny	68.8	70.8	66.2	63.6	67.2
11-Apr-18	10:45	Cloudy	73.0	74.2	70.9		72.5
17-Apr-18	13:00	Cloudy	68.8	70.8	67.3		67.2
23-Apr-18	13:10	Sunny	74.5	77.1	72.3		74.1

Location CM3 - Block S, Yau Lai Estate Phase 5, Yau Tong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
6-Apr-18	11:00	Cloudy	74.1	75.6	72.9	65.6	73.4
11-Apr-18	11:30	Cloudy	74.1	76.2	70.9		73.4
18-Apr-18	10:05	Cloudy	74.1	76.6	70.7		73.4
24-Apr-18	16:15	Cloudy	74.3	76.5	71.5		73.7

Location CM4 - Tin Hau Temple, Cha Kwo Ling							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
3-Apr-18	13:10	Sunny	59.0	61.7	53.4	62.0	59.0 Measured \leq Baseline
11-Apr-18	13:00	Cloudy	65.2	68.3	61.7		62.4
17-Apr-18	15:00	Cloudy	64.2	66.1	61.8		60.2
23-Apr-18	09:10	Sunny	65.6	66.8	60.4		63.1

Location CM5 - CCC Kei Faat Primary School, Yau Tong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
6-Apr-18	10:15	Cloudy	69.5	71.6	66.3	68.2	63.6
11-Apr-18	10:30	Cloudy	69.5	71.6	66.8		63.6
18-Apr-18	10:45	Cloudy	70.5	73.0	66.4		66.6
24-Apr-18	15:00	Cloudy	69.7	71.9	66.4		64.4

Appendix G - Noise Monitoring Results




(0700-1900 hrs on Normal Weekdays)

Location CM6(A) - Site Boundary of Contract No. NE/2015/02 near Tower 1, Ocean Shores							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
3-Apr-18	11:30	Sunny	61.6	65.5	42.3	61.9	61.6 Measured ≤ Baseline
13-Apr-18	14:10	Sunny	66.5	68.3	61.2		64.7
19-Apr-18	09:30	Sunny	68.4	69.0	63.5		67.3
25-Apr-18	14:55	Cloudy	70.1	73.4	62.9		69.4
30-Apr-18	11:30	Cloudy	63.4	65.2	59.5		58.1

Location CM7(A) - Site Boundary of Contract No. NE/2015/02 near Tower 7, Ocean Shores							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
3-Apr-18	10:50	Sunny	70.3	74.3	58.6	58.3	70.0
13-Apr-18	13:25	Sunny	67.3	70.6	60.1		66.7
19-Apr-18	10:45	Sunny	66.8	67.7	60.5		66.1
25-Apr-18	13:30	Cloudy	68.4	69.7	61.3		68.0
30-Apr-18	10:40	Cloudy	63.2	64.8	61.3		61.5




Location CM8(A) - Park Central, L1/F Open Space Area							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
3-Apr-18	14:30	Sunny	64.3	67.8	57.3	69.1	64.3 Measured ≤ Baseline
13-Apr-18	09:05	Sunny	69.5	71.8	61.7		58.9
19-Apr-18	13:45	Sunny	66.4	67.7	62.5		66.4 Measured ≤ Baseline
25-Apr-18	09:30	Cloudy	66.6	67.6	65.7		66.6 Measured ≤ Baseline
30-Apr-18	13:10	Cloudy	63.4	64.9	61.0		63.4 Measured ≤ Baseline

Noise Levels

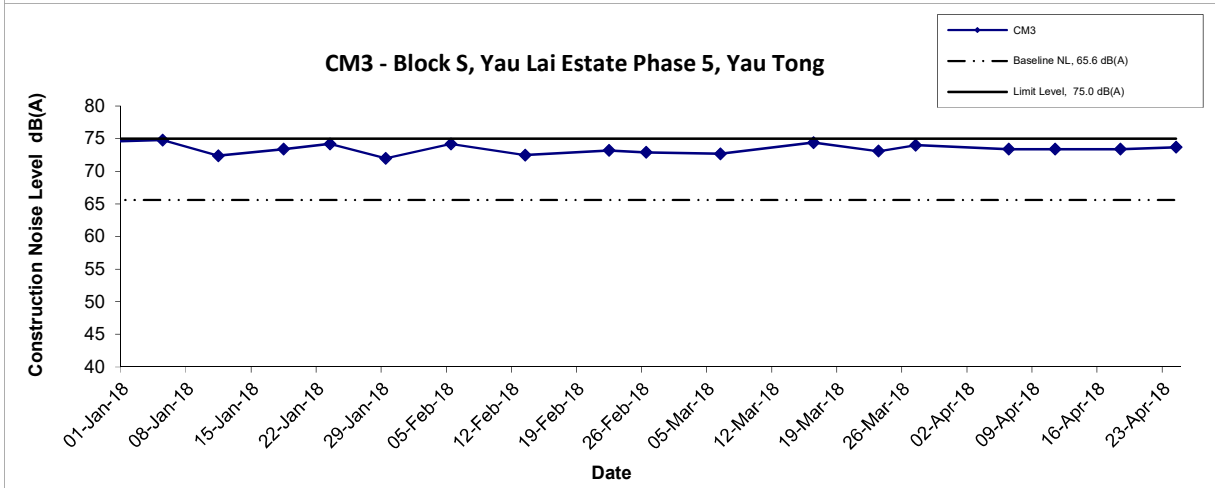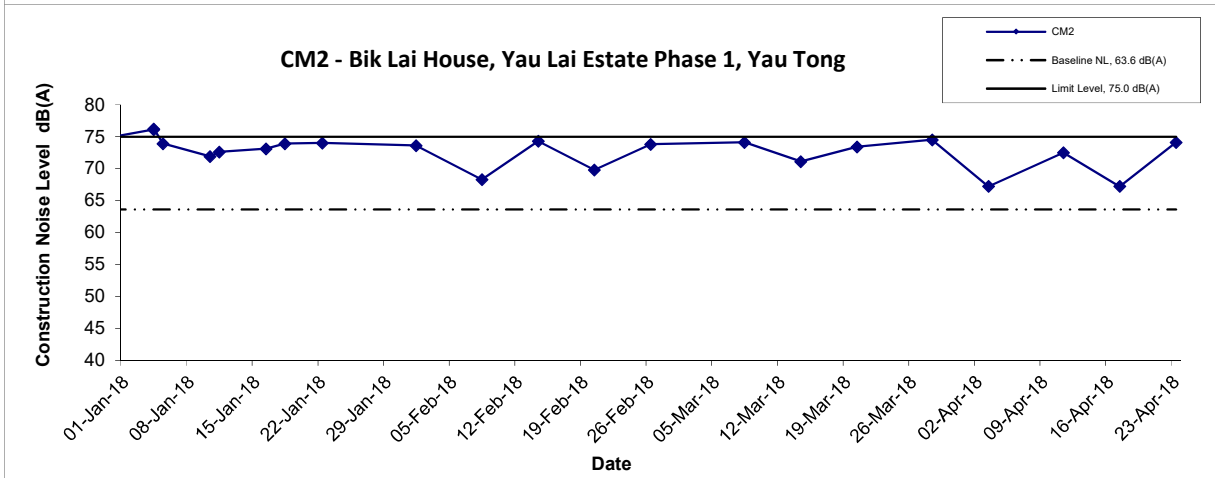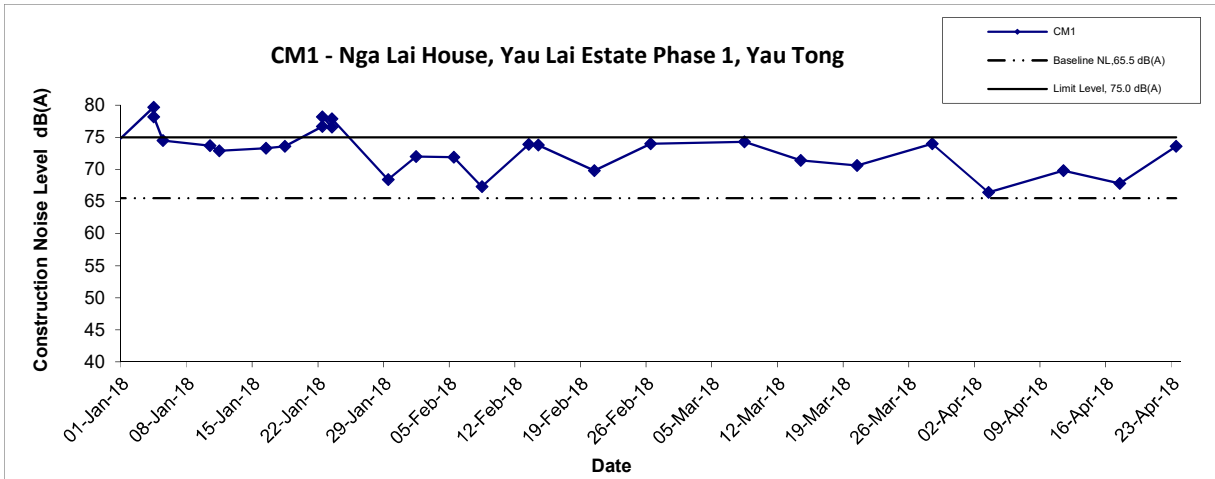



Title Agreement No. CE/59/2015 (EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction Graphical Presentation of Construction Noise Monitoring Results	Scale N.T.S	Project No. MA16034	
	Date Apr 18	Appendix G	

Noise Levels

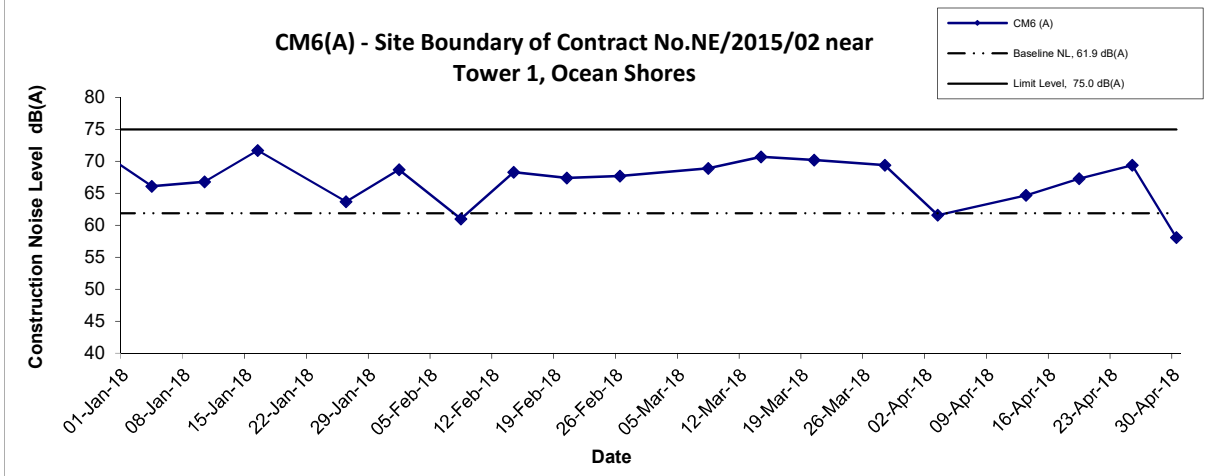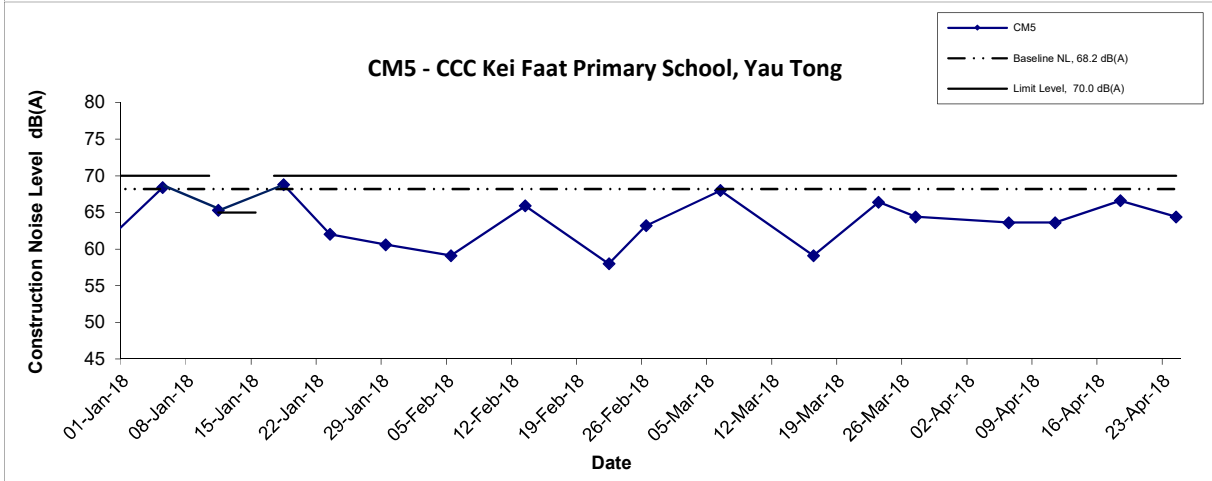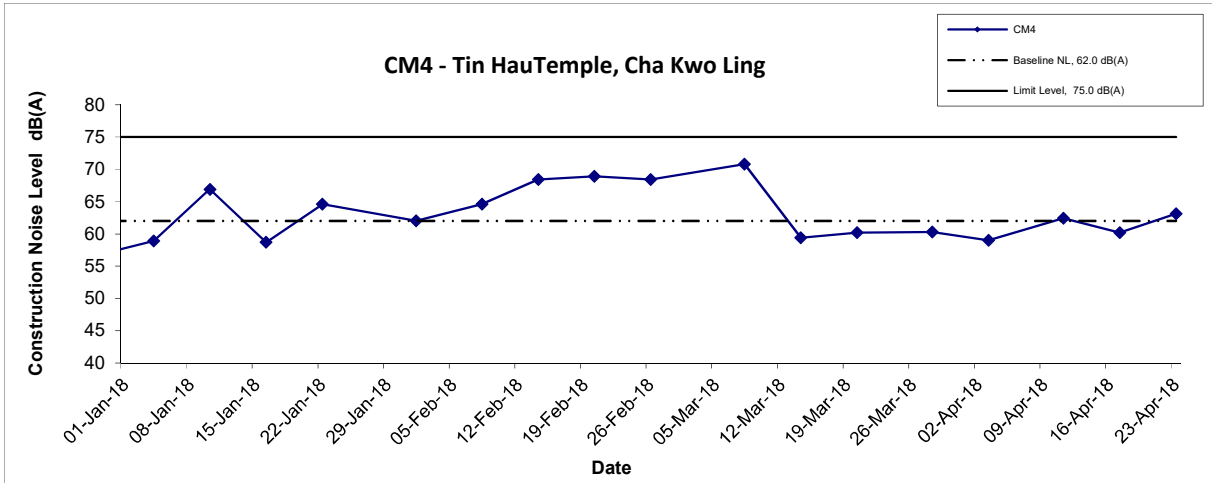

Title Agreement No. CE/59/2015 (EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction Graphical Presentation of Construction Noise Monitoring Results	Scale N.T.S Date Apr 18	Project No. MA16034 Appendix G	
--	--------------------------------------	---	--

Noise Levels

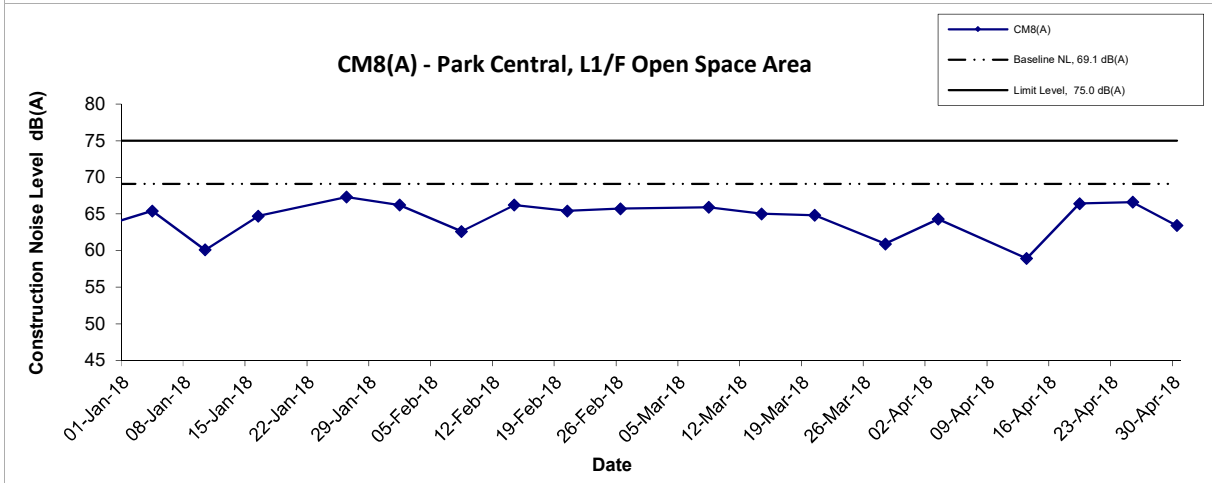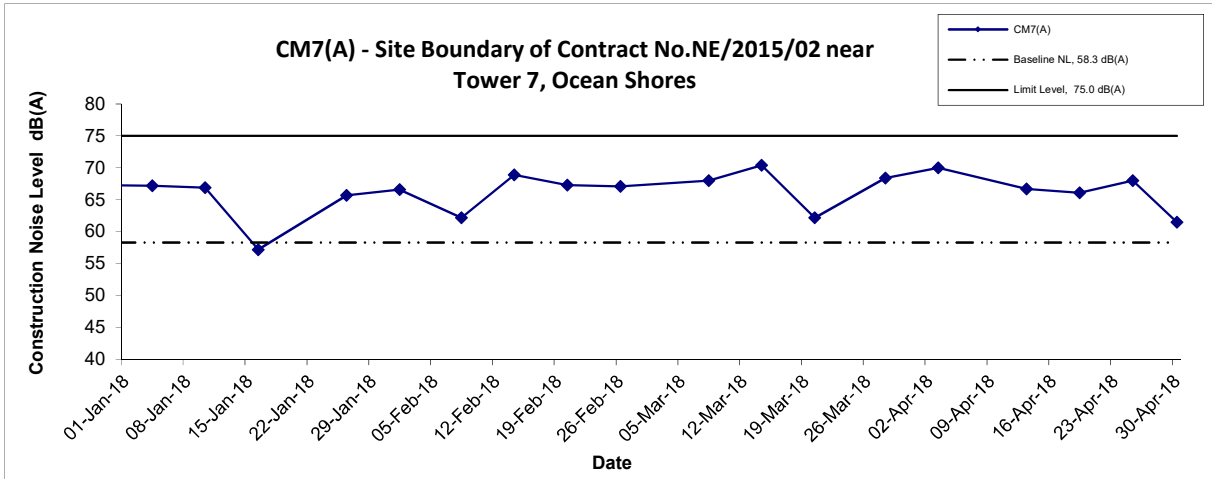

Title Agreement No. CE/59/2015 (EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction Graphical Presentation of Construction Noise Monitoring Results	Scale N.T.S	Project No. MA16034	
	Date Apr 18	Appendix G	

**APPENDIX H
GROUNDWATER QUALITY
MONITORING RESULTS AND
GRAPHICAL PRESENTATIONS**

Agreement No. CE/59/2015 (EP)**Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction****Groundwater Quality Monitoring Results at Stream 1**

Date	Weather Condition	Sampling Time	Depth (m)	Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)	
				Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
11-Apr-18	Sunny	16:38	Middle	28.7	28.7	7.8	7.8	1.2	1.2	101.0	101.0	7.8	7.8	1.4	1.4
				28.7		7.8		1.2		101.0		7.8			
24-Apr-18	Rainy	13:55	Middle	27.8	27.8	8.0	8.0	0.2	0.2	99.2	99.2	7.8	7.8	1.6	1.6
				27.8		8.0		0.2		99.2		7.8			

Groundwater Quality Monitoring Results at Stream 2

Date	Weather Condition	Sampling Time	Depth (m)	Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)	
				Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
11-Apr-18	Sunny	12:37	Middle	28.5	28.5	8.2	8.2	0.3	0.3	99.6	99.6	7.7	7.7	1.9	2.0
				28.5		8.2		0.3		99.6		7.7			
24-Apr-18	Rainy	14:15	Middle	27.0	27.0	8.1	8.1	0.2	0.2	98.0	98.0	7.8	7.8	1.0	1.0
				26.9		8.1		0.2		98.0		7.8			

Groundwater Quality Monitoring Results at Stream 3

Date	Weather Condition	Sampling Time	Depth (m)	Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)	
				Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
24-Apr-18	Rainy	16:38	Middle	27.6	27.7	7.9	7.9	0.4	0.4	101.9	101.9	8.0	8.0	1.4	1.4
				27.7		7.9		0.4		101.8		8.0			

Agreement No. CE/59/2015 (EP)**Environmental Team for Tseung Kwan O - Lam Tin Tunnel - Design and Construction****Summary of Groundwater Quality Monitoring Results**

Location	Date	Parameters (unit)								
		pH	Dissolved Oxygen (mg/L)	Turbidity (NTU)	SS (mg/L)	BOD ₅ (mg O ₂ /L)	TOC (mg-TOC/L)	Total Nitrogen (mg/L)	NH ₃ -N (mg NH ₃ -N/L)	Total Phosphorus (mg-P/L)
Stream 1	11-Apr-18	7.8	7.8	1.4	3	<2	3	<0.6	<0.05	<0.05
	24-Apr-18	8	7.8	1.6	6.0	4	12	3.7	<0.05	0.06
Stream 2	11-Apr-18	8.2	7.7	2.0	3	<2	5	0.9	<0.05	<0.05
	24-Apr-18	8.1	7.8	1.0	6	8	16	2.9	0.07	0.08
Stream 3	24-Apr-18	7.9	8	1.4	3.0	4	8	2.9	0.16	0.1

TEST REPORT

APPLICANT: Cinotech Consultants Limited
1710, Technology Park,
18 On Lai Street,
Shatin, N.T.

Report No.:	28692
Date of Issue:	2018-04-20
Date Received:	2018-04-11
Date Tested:	2018-04-11
Date Completed:	2018-04-20

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Sample Description : 2 liquid samples as received from client said to be groundwater
Laboratory No. : 28692
Project No. : MA16034 (Groundwater)
Project Name : Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O –
 Lam Tin Tunnel – Design and Construction
Custody No. : MA16034(Groundwater)/20180411
Sampling Date : 2018-04-11

Tests Requested & Methodology:

Item	Parameters	Ref. Method	Limit of reporting
1	Total Suspended Solids	APHA 17ed 2540 D	*0.5 mg/L
2	Biochemical Oxygen Demand	APHA 19ed 5210B	2 mg O ₂ /L
3	Total Organic Carbon	In-house method SOP020 (Wet Oxidation)	1 mg-TOC/L
4	Nitrogen (Total Kjeldahl + nitrate + nitrite)	In-house method SOP063 (FIA)	0.6 mg N/L
5	Ammonia	In-house method SOP057 (FIA)	0.05 mg NH ₃ -N/L
6	Total Phosphorus	In-house method SOP055 (FIA)	0.05 mg-P/L

Results:

Sample ID	Stream 1	Stream 2
Sampling Depth	S	S
Sample No.	28692-1	28692-2
Total Suspended Solids (mg/L)	3	3
Biochemical Oxygen Demand (mg O ₂ /L)	<2	<2
Total Organic Carbon (mg-TOC/L)	3	5
Nitrogen (Total Kjeldahl + nitrate + nitrite) (mg N/L)	<0.6	0.9
Ammonia (mg NH ₃ -N/L)	<0.05	<0.05
Total Phosphorus (mg-P/L)	<0.05	<0.05

Remarks: 1) <= less than
 2) S = Surface, M = Middle, B = Bottom
 3) * Limit of Reporting is reported as Detection Limit

*****END OF REPORT*****

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**


PATRICK TSE
 Laboratory Manager

TEST REPORT

APPLICANT: Cinotech Consultants Limited
1710, Technology Park,
18 On Lai Street,
Shatin, N.T.

Report No.:	28772
Date of Issue:	2018-05-04
Date Received:	2018-04-24
Date Tested:	2018-04-24
Date Completed:	2018-05-04

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Sample Description : 3 liquid samples as received from client said to be groundwater
Laboratory No. : 28772
Project No. : MA16034 (Groundwater)
Project Name : Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O –
Lam Tin Tunnel – Design and Construction
Custody No. : MA16034(Groundwater)/20180424
Sampling Date : 2018-04-24

Tests Requested & Methodology:

Item	Parameters	Ref. Method	Limit of reporting
1	Total Suspended Solids	APHA 17ed 2540 D	*0.5 mg/L
2	Biochemical Oxygen Demand	APHA 19ed 5210B	2 mg O ₂ /L
3	Total Organic Carbon	In-house method SOP020 (Wet Oxidation)	1 mg-TOC/L
4	Nitrogen (Total Kjeldahl + nitrate + nitrite)	In-house method SOP063 (FIA)	0.6 mg N/L
5	Ammonia	In-house method SOP057 (FIA)	0.05 mg NH ₃ -N/L
6	Total Phosphorus	In-house method SOP055 (FIA)	0.05 mg-P/L

Results:

Sample ID	Stream 1	Stream 2	Stream 3
Sampling Depth	S	S	S
Sample No.	28772-1	28772-2	28772-3
Total Suspended Solids (mg/L)	6	6	3
Biochemical Oxygen Demand (mg O ₂ /L)	4	8	4
Total Organic Carbon (mg-TOC/L)	12	16	8
Nitrogen (Total Kjeldahl + nitrate + nitrite) (mg N/L)	3.7	2.9	2.9
Ammonia (mg NH ₃ -N/L)	<0.05	0.07	0.16
Total Phosphorus (mg-P/L)	0.06	0.08	0.10

Remarks: 1) <= less than
2) S = Surface, M = Middle, B = Bottom
3) * Limit of Reporting is reported as Detection Limit




*****END OF REPORT*****

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

pH

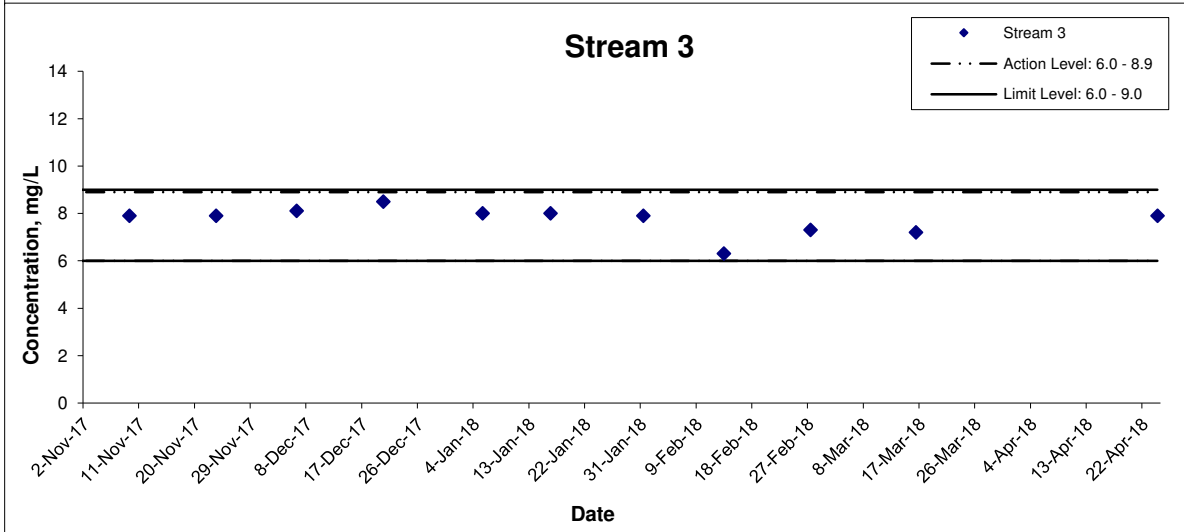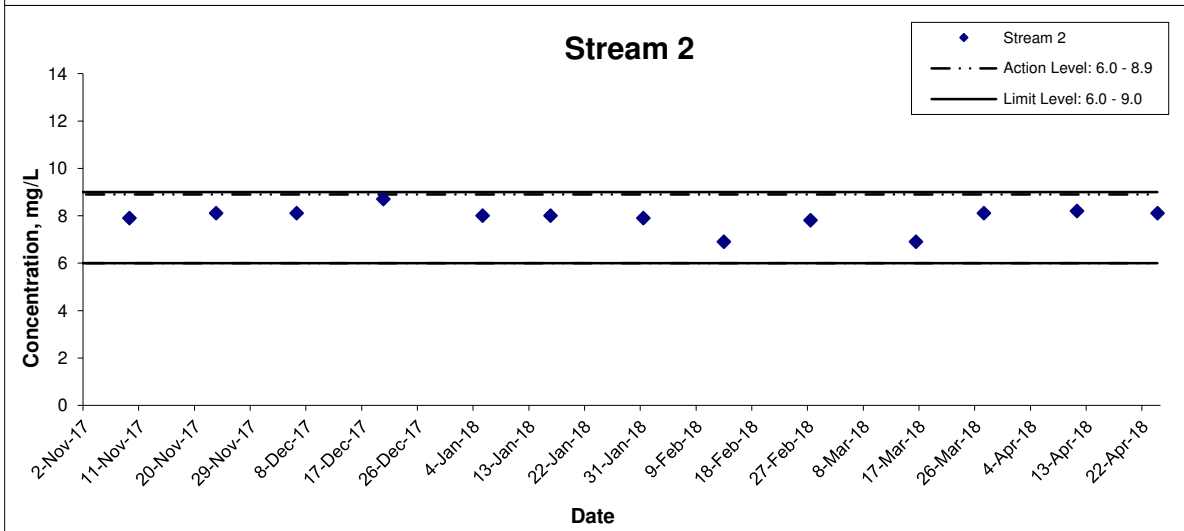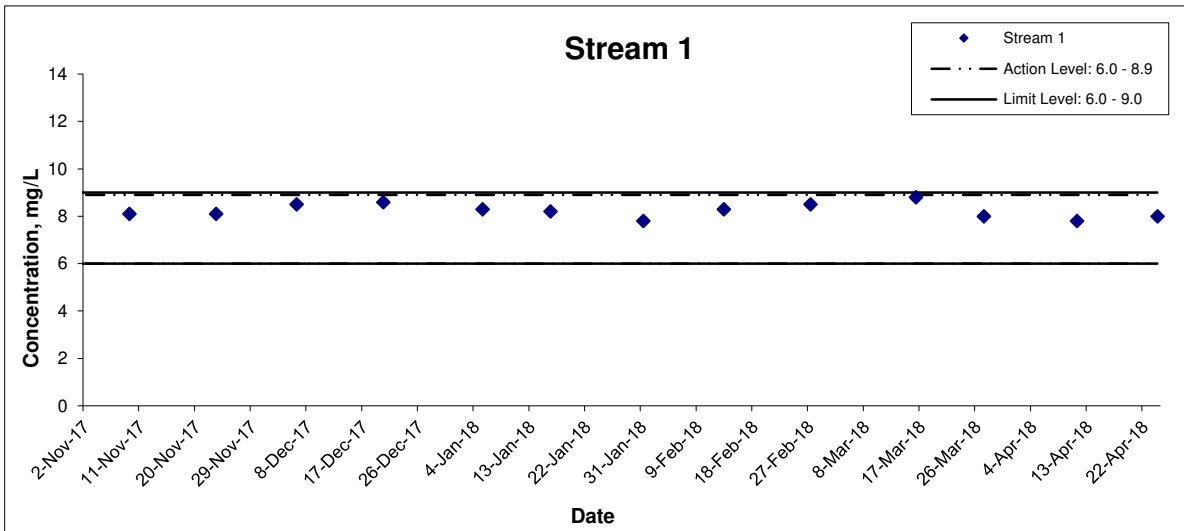




Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result	Scale N.T.S	Project No. MA16034	
	Date Apr 18	Appendix H	

Dissolved Oxygen

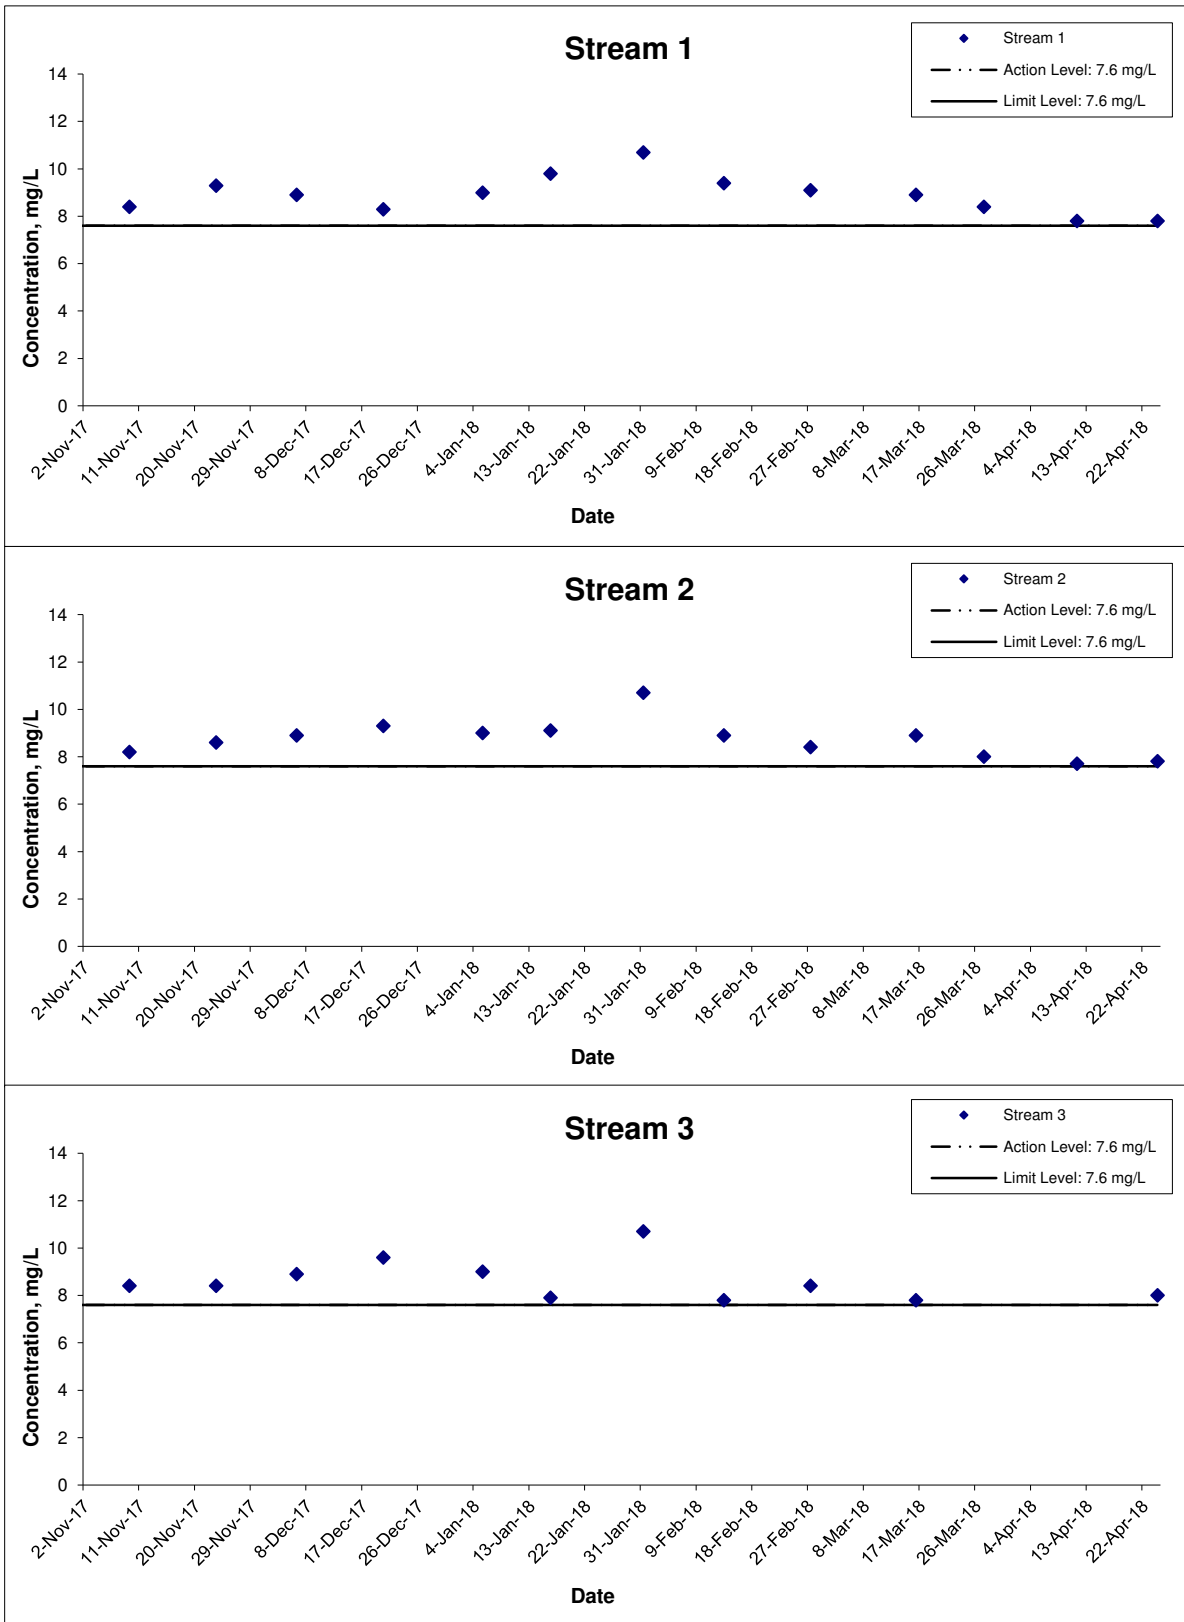


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result	Scale N.T.S	Project No. MA16034	
	Date Apr 18	Appendix H	

Turbidity

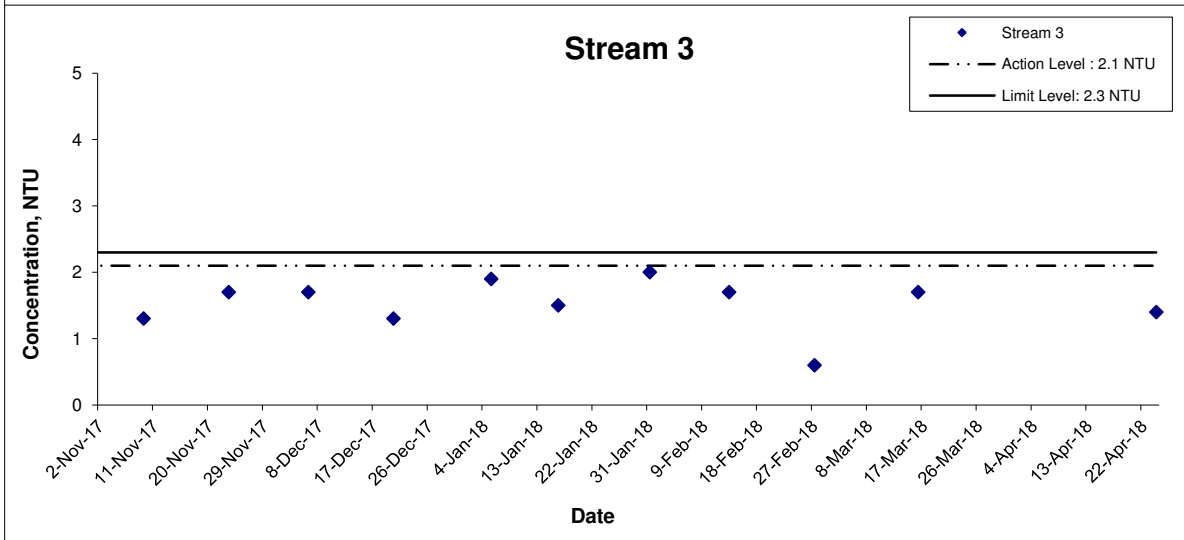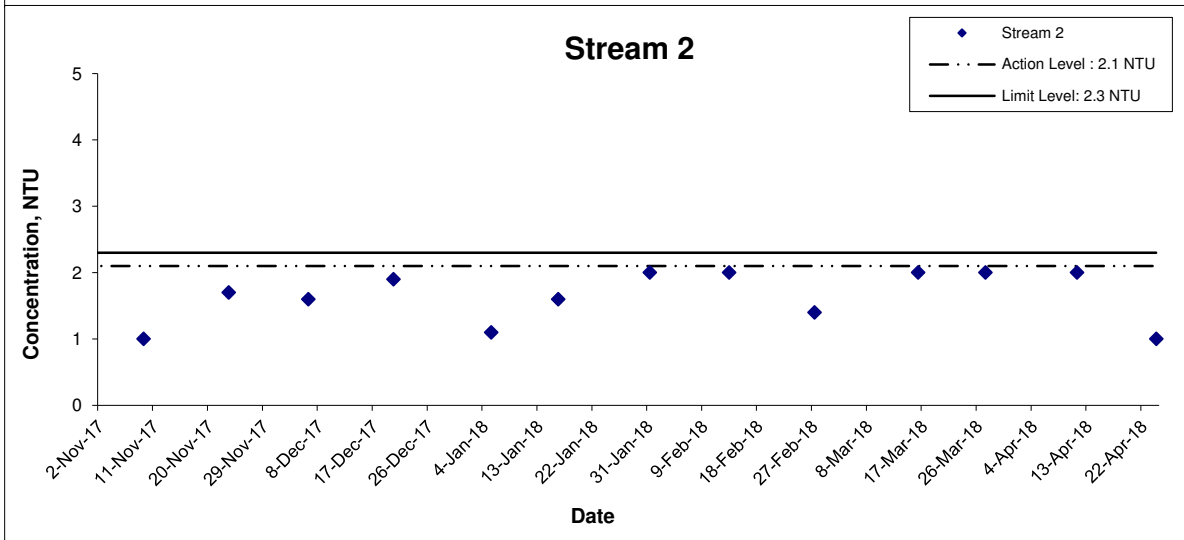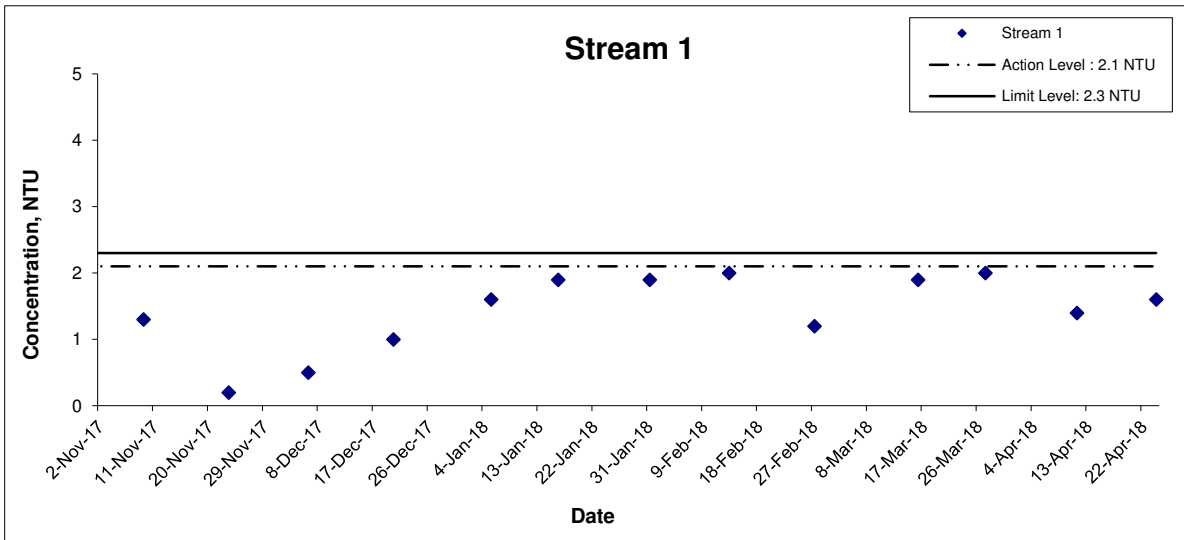


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result	Scale N.T.S	Project No. MA16034	
	Date Apr 18	Appendix H	

Suspended Solids

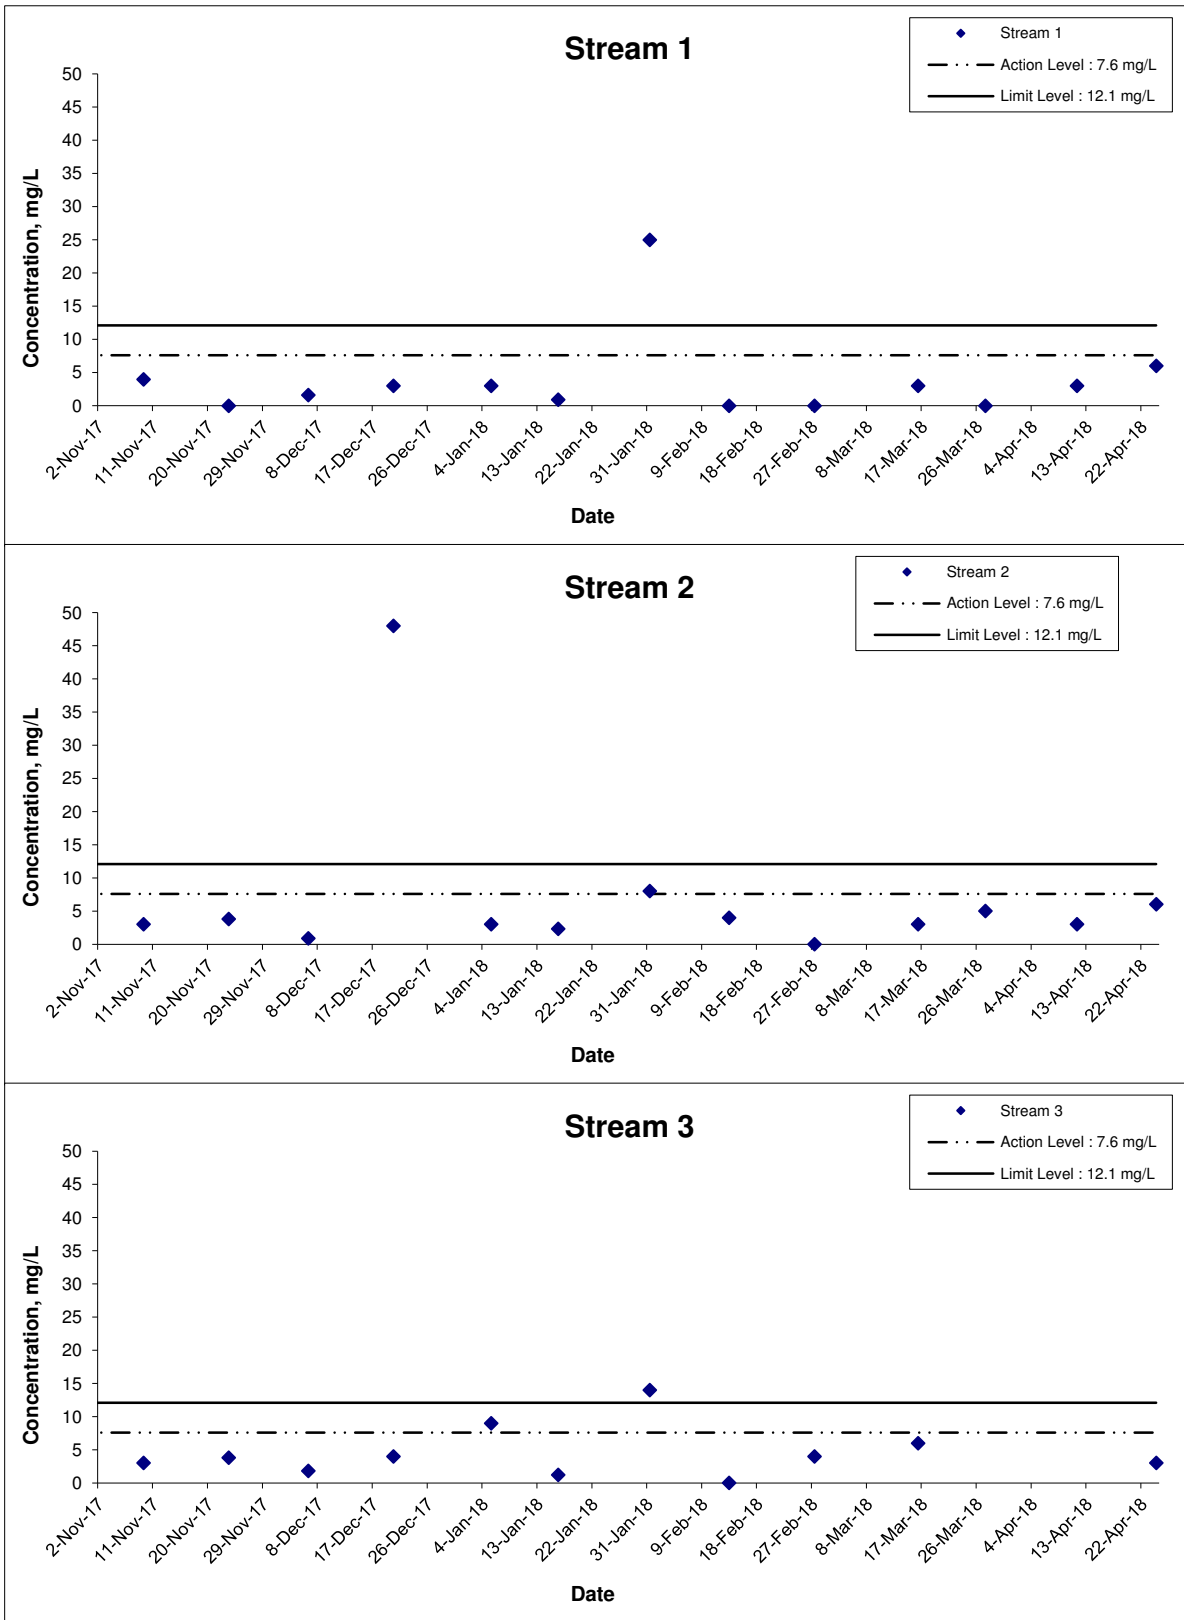

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result	Scale N.T.S	Project No. MA16034	
	Date Apr 18	Appendix H	




5-day Biochemical Oxygen Demand (BOD₅)

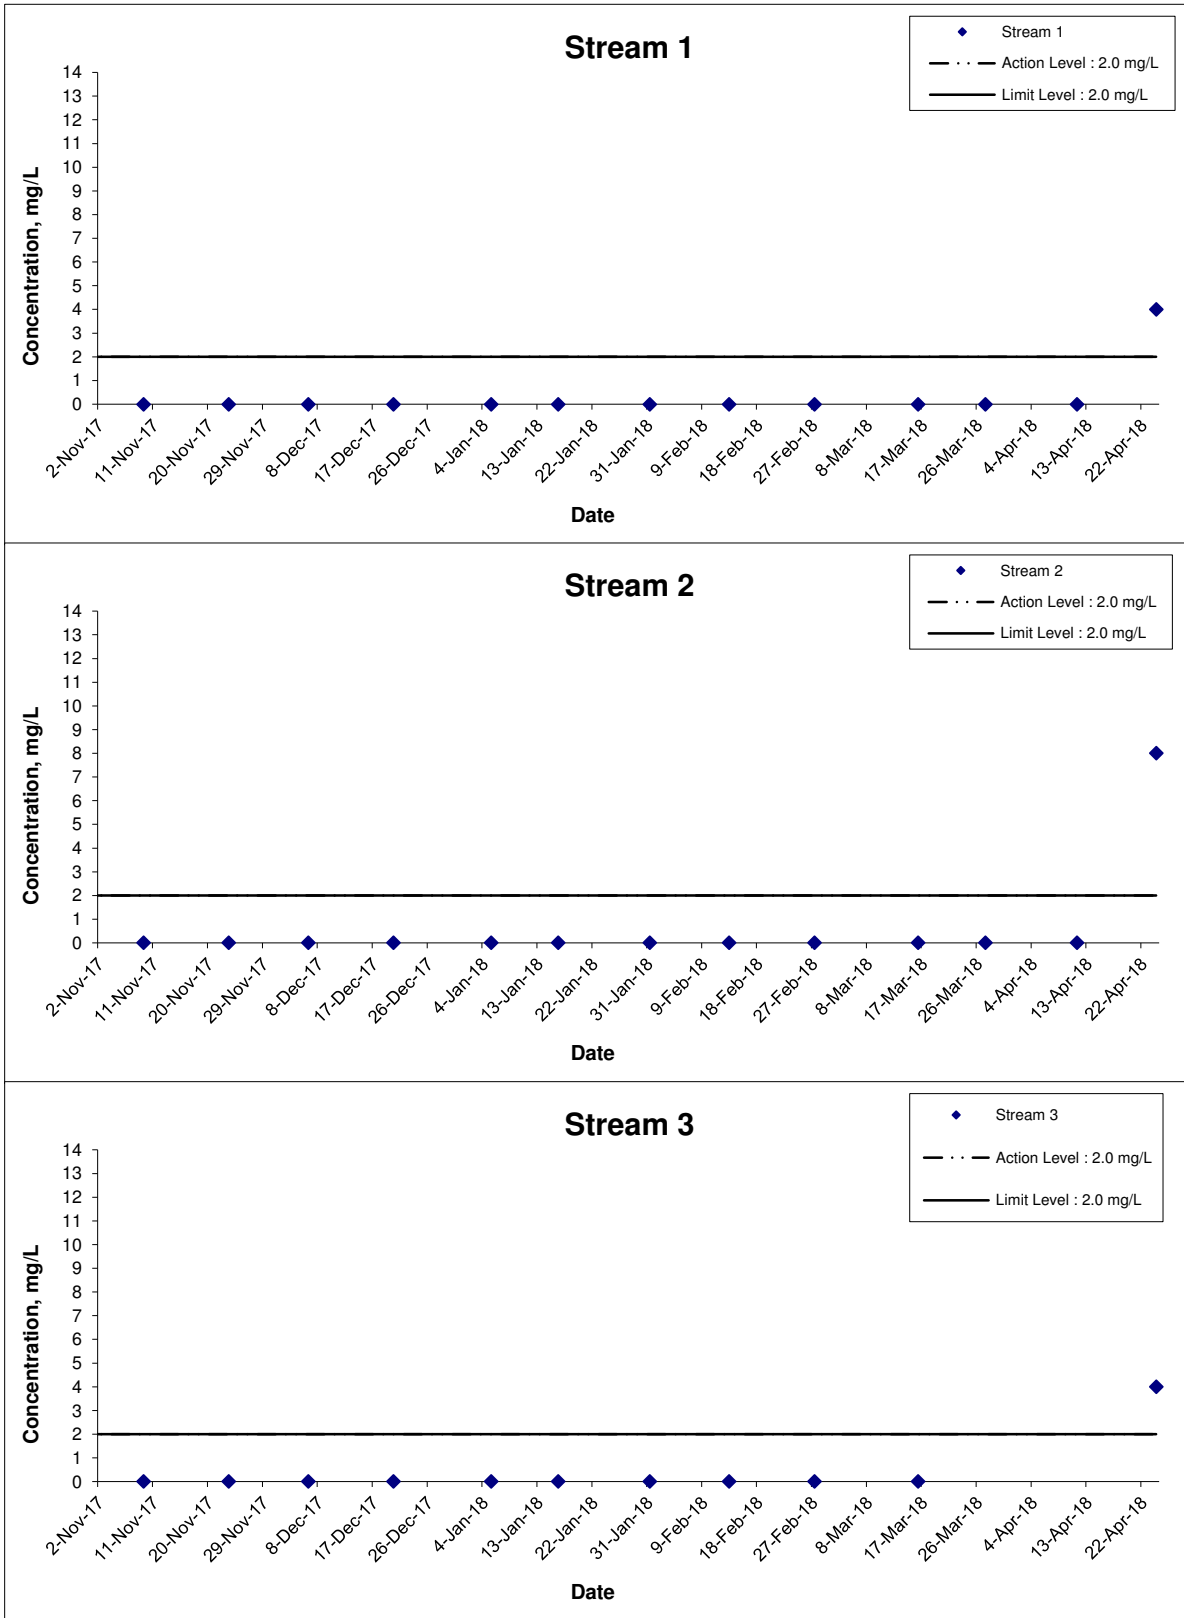

Remarks: The graphical point at zero concentration is presented as <2 mg/L


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result	Scale N.T.S	Project No. MA16034	CINOTECH
	Date Apr 18	Appendix H	

Total Organic Carbon (TOC)

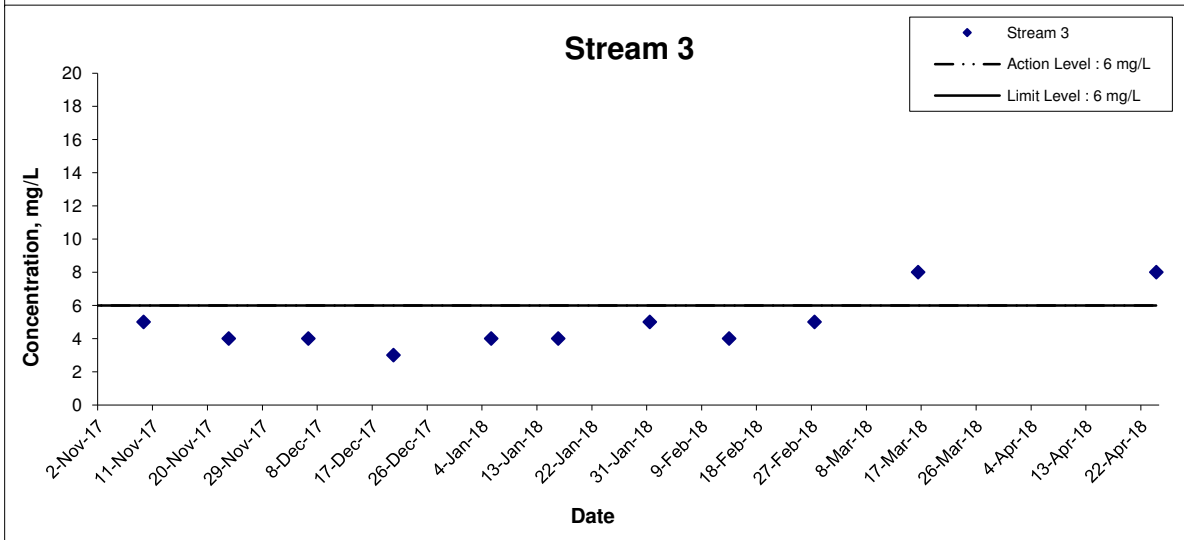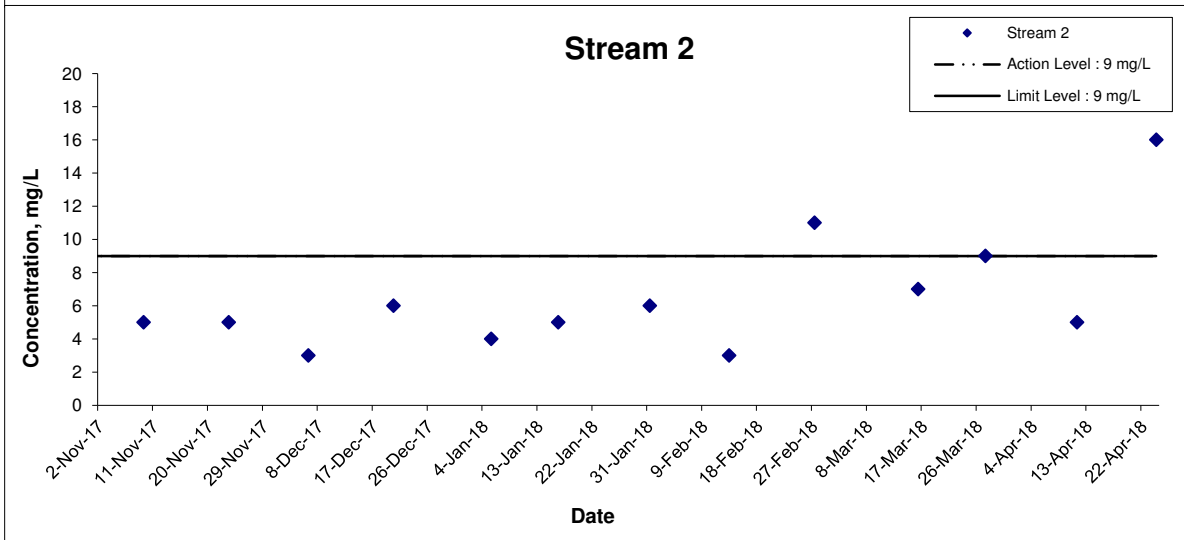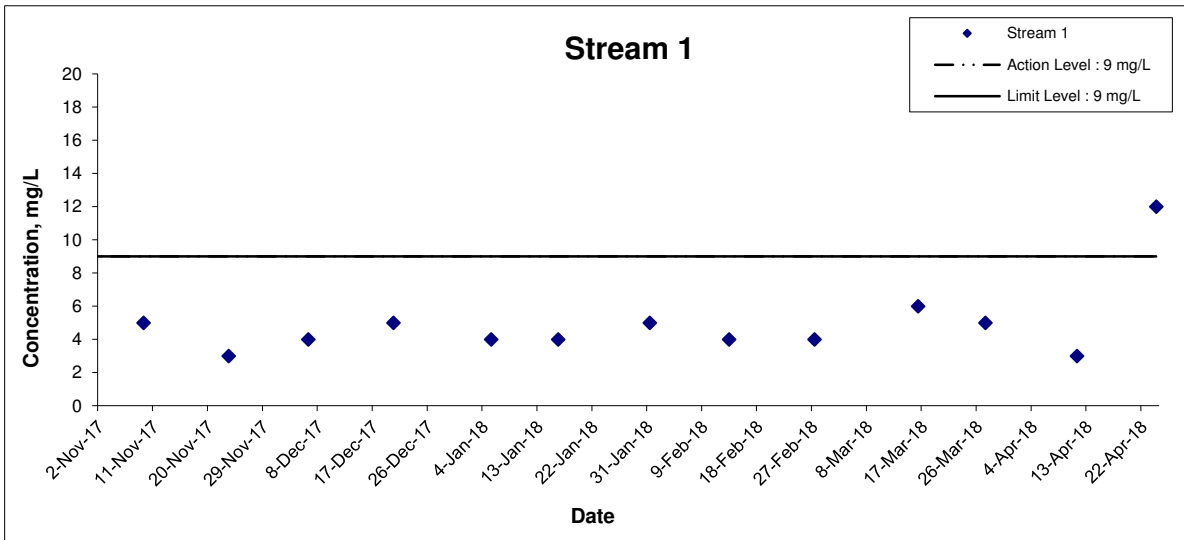

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result	Scale N.T.S	Project No. MA16034	
	Date Apr 18	Appendix H	


Total Nitrogen

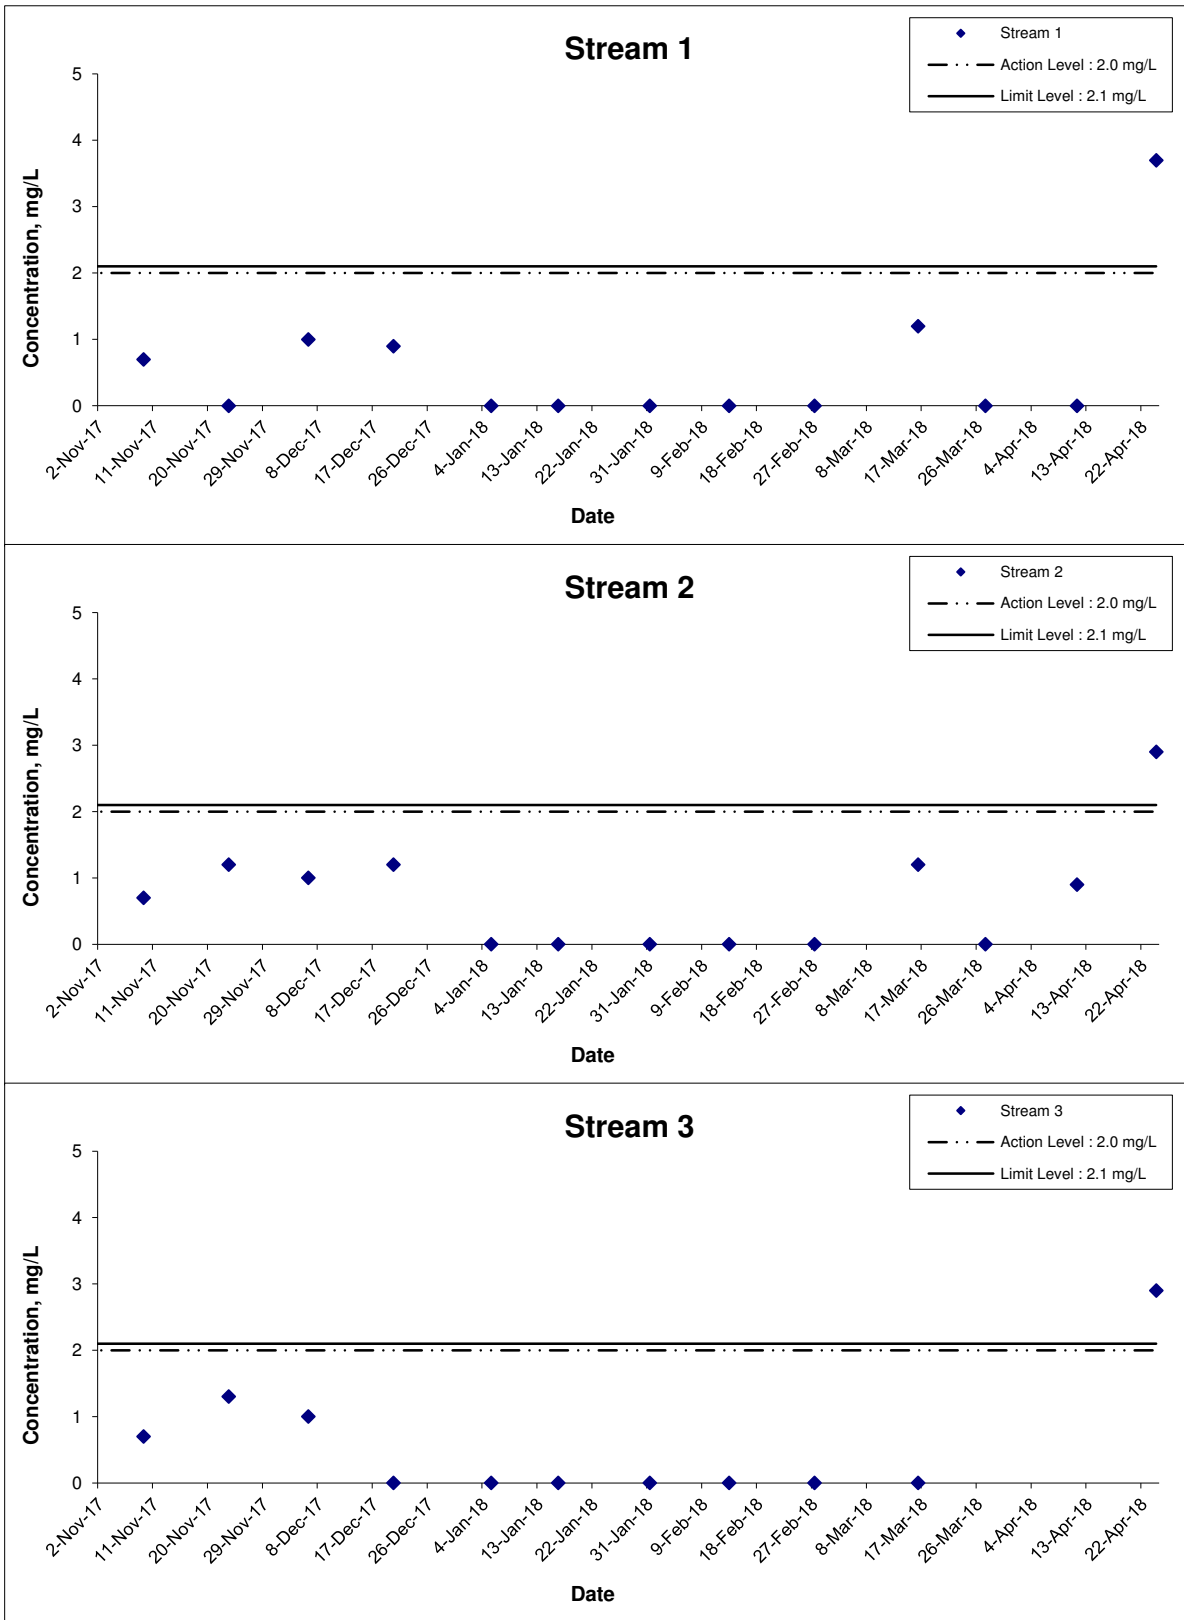

Remarks: The graphical point at zero concentration is presented as <0.6 mg/L

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result	Scale	Project No.	
	Date	Appendix	
	N.T.S	MA16034	
	Apr 18	H	


Ammonia-Nitrogen

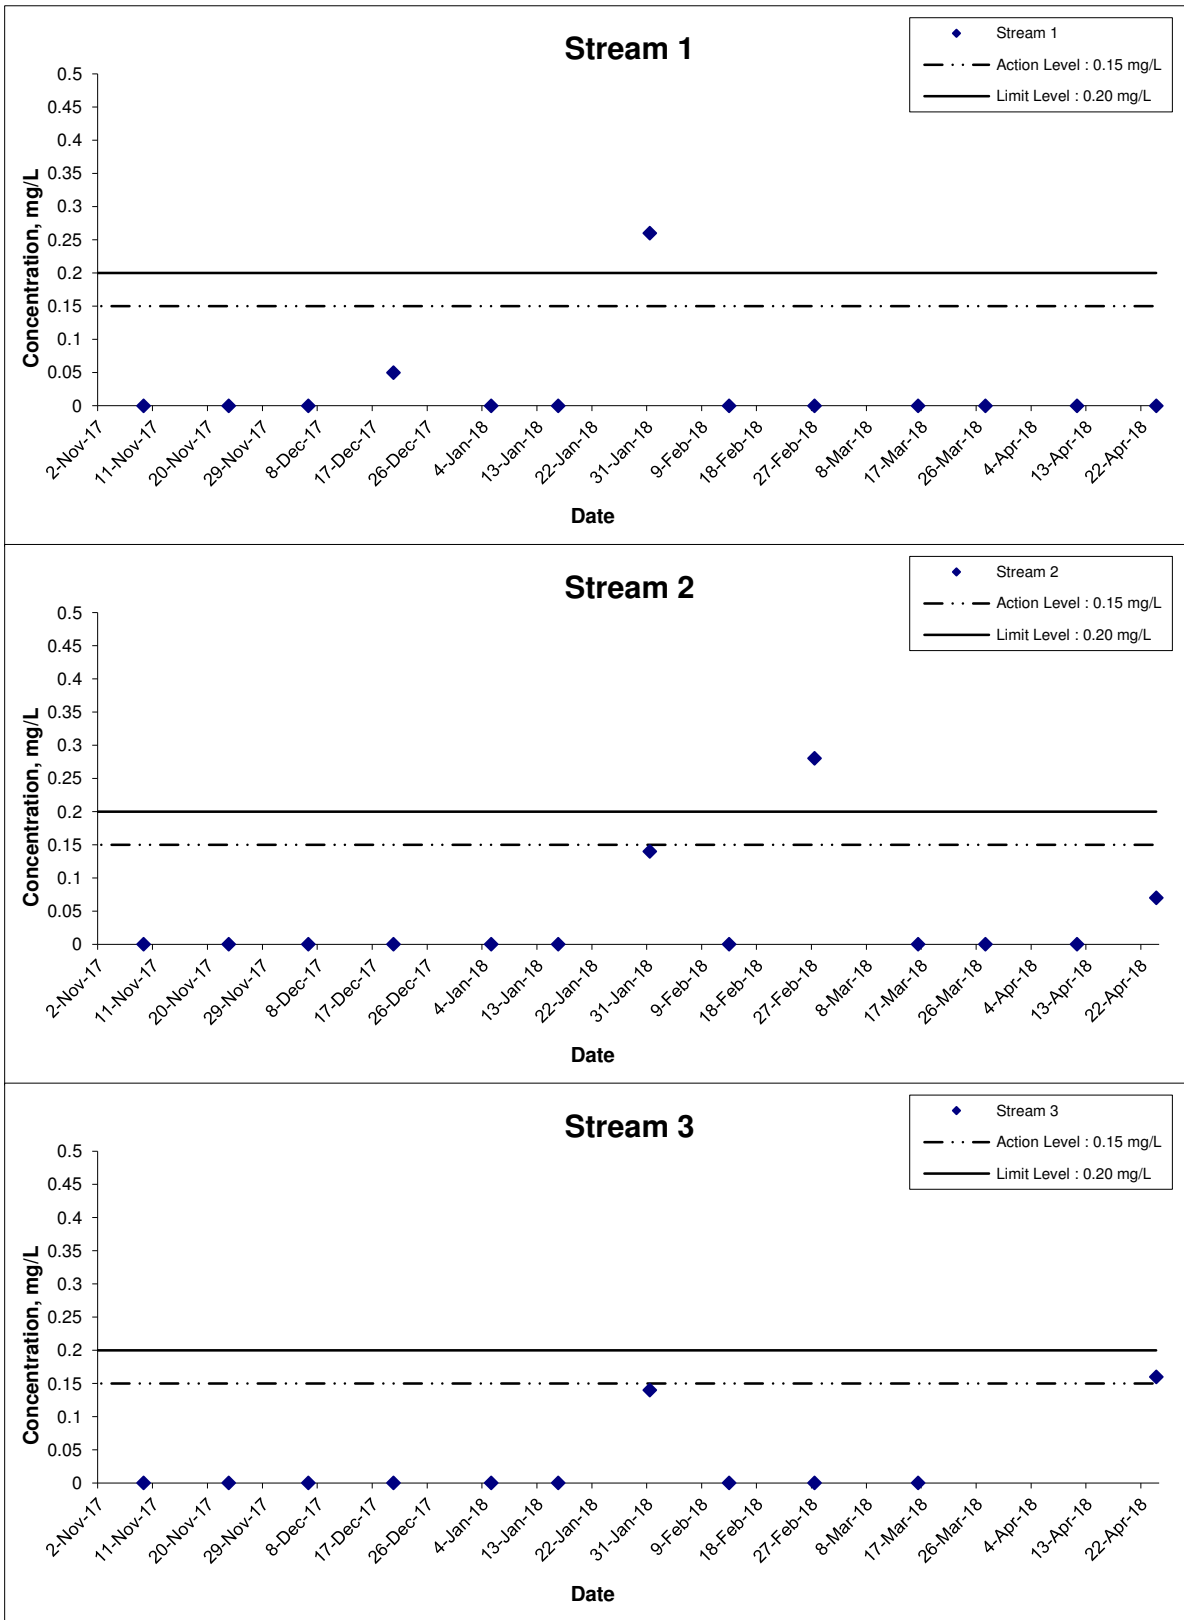

Remarks: The graphical point at zero concentration is presented as <0.05 mg/L

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result	Scale N.T.S	Project No. MA16034	CINOTECH
	Date Apr 18	Appendix H	

Total Phosphate

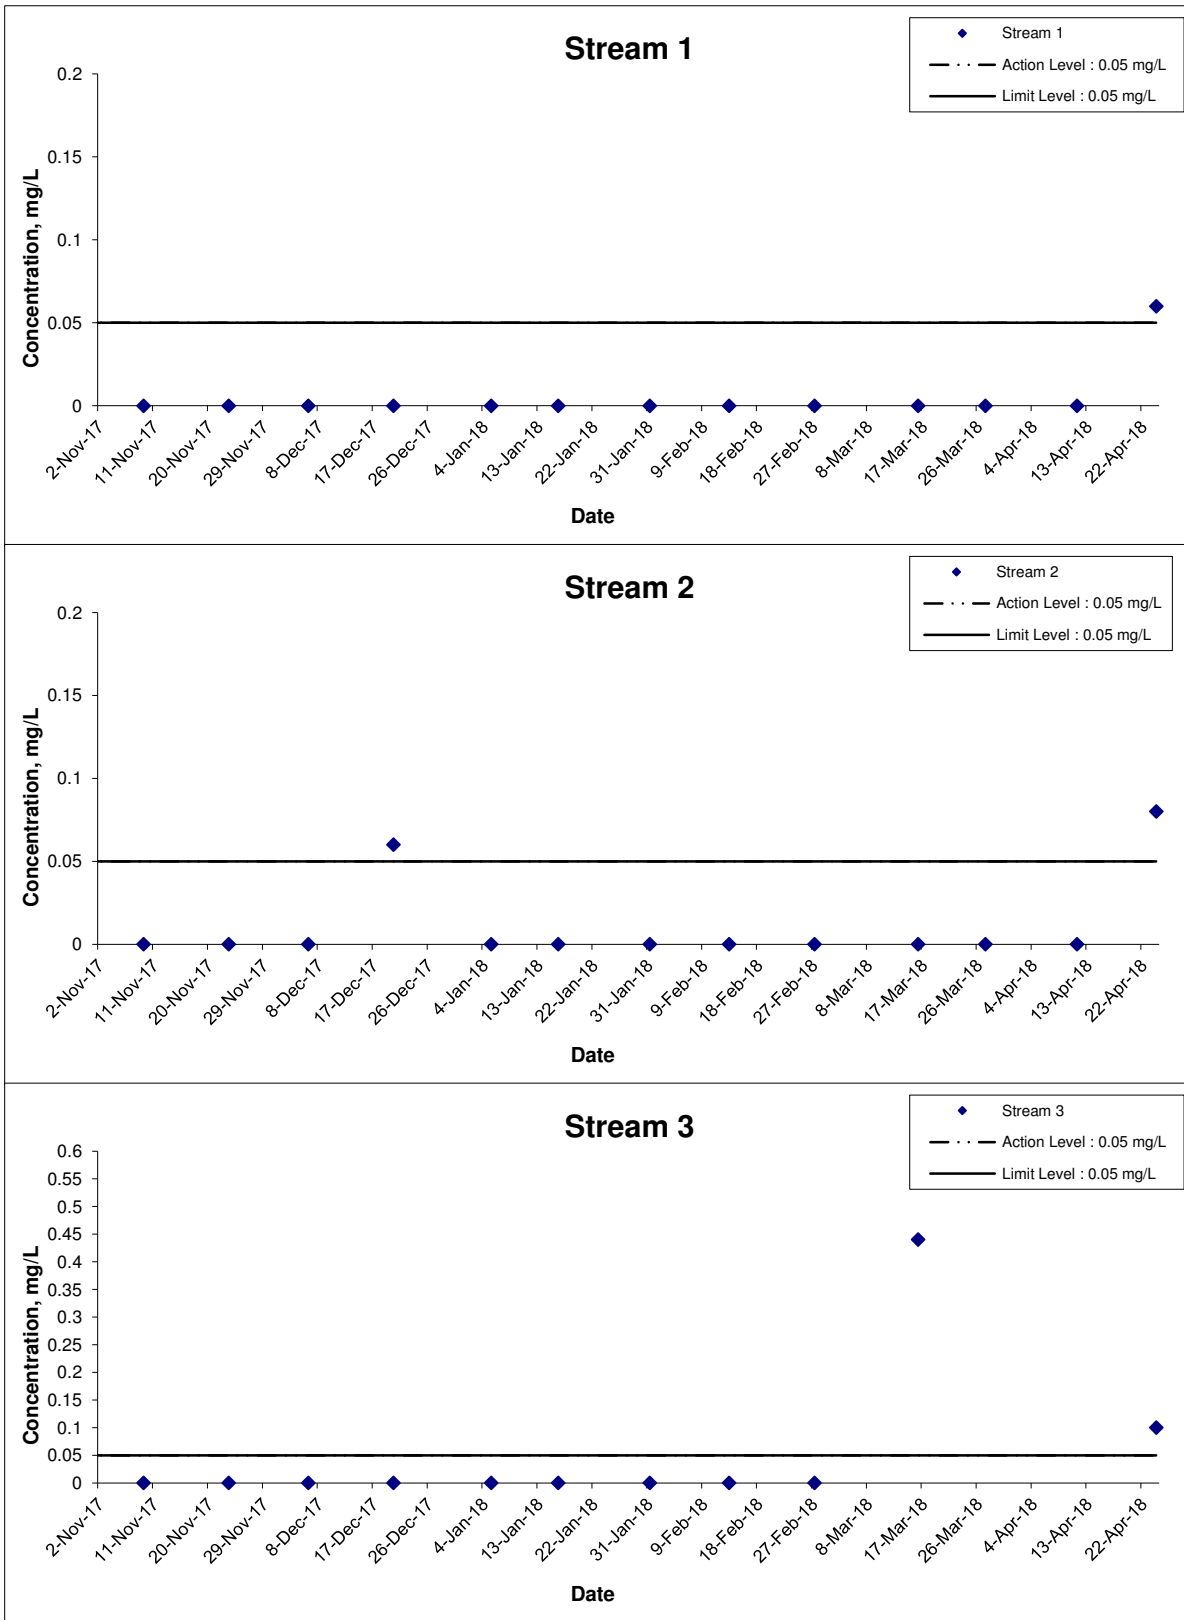

Remarks: The graphical point at zero concentration is presented as <0.05 mg/L

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction Graphical Presentation of Groundwater Quality Monitoring Result	Scale N.T.S	Project No. MA16034	
	Date Apr 18	Appendix H	



Photo 1



Photo 2

Remark: No groundwater quality monitoring was conducted for stream 3 on 11 April 2018 due to the drying out of stream water on that day. (See Photo 1 & 2)

**APPENDIX I
MARINE WATER QUALITY
MONITORING RESULTS AND
GRAPHICAL PRESENTATIONS**

Appendix I - Action and Limit Levels for Marine Water Quality on 4 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 5.9 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 6.4 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.5 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.0 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.5 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.0 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.7 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.3 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 04 April 2018**

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
C1	Sunny	Moderate	16:06	Surface	1	22.6 22.5	22.6	8.2 8.2	8.2	33.3 33.4	33.4	104.3 103.2	103.8	7.3 7.3	7.3	7.3	7.3	2.6 2.7	2.7	3.8	5.0 5.1	5.1	4.0
				Middle	9	21.3 21.6	21.5	8.1 8.2	8.2	34.3 34.2	34.3	106.1 102.8	104.5	7.2 7.1	7.2	7.1	3.8 3.5	3.7	3.5 3.4		3.5		
				Bottom	17	20.3 19.8	20.1	8.2 8.2	8.2	34.0 34.6	34.3	101.8 100.0	100.9	7.1 6.9	7.0	7.0	4.9 5.0	5.0	4.9 5.0		3.4		
C2	Sunny	Moderate	14:37	Surface	1	22.6 22.6	22.6	8.3 8.2	8.3	33.6 33.7	33.7	111.6 111.3	111.5	7.7 7.7	7.7	7.4	7.4	2.4 2.4	2.4	3.8	5.4 5.4	5.4	4.3
				Middle	16.5	21.2 20.9	21.1	8.2 8.1	8.2	34.5 34.1	34.3	96.5 108.5	102.5	6.7 7.5	7.1	7.1	4.1 4.2	4.2	2.0 2.0		2.0		
				Bottom	32	20.6 20.5	20.6	8.1 8.1	8.1	34.6 33.9	34.3	88.8 89.2	89.0	6.2 6.2	6.2	6.2	4.8 4.9	4.9	5.5 5.6		5.6		
G1	Sunny	Moderate	15:19	Surface	1	23.8 23.8	23.8	8.3 8.3	8.3	33.5 33.5	33.5	112.9 114.1	113.5	7.8 7.8	7.8	7.6	7.6	2.8 2.7	2.8	2.7	2.6 2.5	2.6	3.3
				Middle	3.5	23.1 23.3	23.2	8.2 8.2	8.2	33.6 33.6	33.6	108.5 106.3	107.4	7.5 7.3	7.4	7.4	2.4 2.4	2.4	4.6 4.6		4.6		
				Bottom	6	22.3 22.3	22.3	8.3 8.2	8.3	34.1 34.0	34.1	103.2 104.3	103.8	7.2 7.2	7.2	7.2	2.9 3.0	3.0	2.7 2.8		2.8		
G2	Sunny	Moderate	15:08	Surface	1	23.2 23.7	23.5	8.2 8.2	8.2	33.5 33.4	33.5	114.0 113.6	113.8	7.8 7.8	7.8	7.7	7.7	2.3 2.3	2.3	2.6	2.2 2.1	2.2	3.4
				Middle	4.5	22.6 22.6	22.6	8.2 8.3	8.3	33.8 33.8	33.8	107.8 107.3	107.6	7.5 7.4	7.5	7.5	2.3 2.4	2.4	3.9 3.8		3.9		
				Bottom	8	21.9 22.3	22.1	8.2 8.2	8.2	34.7 34.1	34.4	106.1 105.6	105.9	7.4 7.3	7.4	7.4	3.0 3.0	3.0	4.2 4.2		4.2		
G3	Sunny	Moderate	15:27	Surface	1	24.0 24.2	24.1	8.2 8.2	8.2	33.1 33.1	33.1	100.5 99.1	99.8	7.0 6.9	7.0	6.8	6.8	2.4 2.4	2.4	2.5	3.0 3.0	3.0	5.2
				Middle	3.5	22.9 22.9	22.9	8.2 8.2	8.2	33.6 33.6	33.6	92.3 92.8	92.6	6.4 6.5	6.5	6.5	2.3 2.4	2.4	6.2 6.0		6.1		
				Bottom	6	22.4 22.3	22.4	8.2 8.2	8.3	33.9 34.0	34.0	95.1 94.6	94.9	6.6 6.6	6.6	6.6	2.7 2.7	2.7	6.5 6.6		6.6		
G4	Sunny	Moderate	15:38	Surface	1	23.3 23.5	23.4	8.3 8.3	8.3	33.6 33.5	33.6	111.5 109.7	110.6	7.7 7.6	7.7	7.5	7.5	2.4 2.3	2.4	3.1	4.5 4.6	4.6	4.8
				Middle	4	22.8 22.8	22.8	8.2 8.2	8.2	33.7 33.7	33.7	103.3 102.5	102.9	7.2 7.1	7.2	7.2	2.4 2.4	2.4	5.4 5.4		5.4		
				Bottom	7	21.6 21.6	21.6	8.1 8.1	8.1	34.3 34.3	34.3	104.8 104.9	104.9	7.3 7.3	7.3	7.3	4.6 4.5	4.6	4.4 4.4		4.4		
M1	Sunny	Moderate	15:15	Surface	1	23.7 23.7	23.7	8.2 8.2	8.2	33.5 33.5	33.5	106.7 111.1	108.9	7.4 7.6	7.5	7.4	7.4	2.4 2.4	2.4	2.4	3.7 3.6	3.7	5.2
				Middle	3	22.9 23.2	23.1	8.2 8.2	8.2	33.6 33.6	33.6	106.3 104.7	105.5	7.3 7.2	7.3	7.3	2.4 2.3	2.4	7.5 7.5		7.5		
				Bottom	5	22.4 22.5	22.5	8.3 8.3	8.3	33.9 33.9	33.9	96.2 97.9	97.1	6.7 6.8	6.8	6.8	2.4 2.6	2.5	4.4 4.5		4.5		
M2	Sunny	Moderate	14:58	Surface	1	23.2 24.1	23.7	8.2 8.3	8.3	33.6 33.3	33.5	109.3 111.9	110.6	7.5 7.7	7.6	7.5	7.5	2.5 2.4	2.5	2.6	4.5 4.3	4.4	4.3
				Middle	5.5	22.3 22.3	22.3	8.3 8.3	8.3	34.0 34.0	34.0	105.3 106.5	105.9	7.3 7.4	7.4	7.4	2.6 2.5	2.6	4.0 4.0		4.0		
				Bottom	10	22.2 22.2	22.2	8.2 8.2	8.2	34.2 34.2	34.2	89.8 91.2	90.5	6.3 6.4	6.4	6.4	2.7 2.8	2.8	4.5 4.5		4.5		
M3	Sunny	Moderate	15:31	Surface	1	24.1 22.4	23.3	8.2 8.3	8.3	33.1 32.1	32.6	102.0 100.0	101.0	7.1 6.9	7.0	6.6	6.6	2.4 2.5	2.5	2.7	2.7 2.7	2.7	3.8
				Middle	3.5	23.0 21.6	22.3	8.2 8.2	8.2	33.5 32.2	32.9	87.1 85.8	86.5	6.1 6.0	6.1	6.1	2.5 2.5	2.5	6.1 5.9		6.0		
				Bottom	6	22.3 20.9	21.6	8.2 8.3	8.3	34.0 32.7	33.4	96.0 95.7	95.9	6.7 6.7	6.7	6.7	3.0 2.9	3.0	2.6 2.6		2.6		
M4	Sunny	Moderate	14:46	Surface	1	24.2 22.4	23.3	8.2 8.3	8.3	33.3 33.0	33.2	110.0 109.3	109.7	7.6 7.5	7.6	7.5	7.5	2.3 2.3	2.3	3.1	4.0 3.9	4.0	3.6
				Middle	5	22.5 22.5	22.5	8.3 8.3	8.3	34.0 34.0	34.0	104.2 104.4	104.3	7.2 7.3	7.3	7.3	2.4 2.4	2.4	2.4 2.5		2.5		
				Bottom	9	22.1 22.3	22.2	8.2 8.2	8.2	34.5 34.2	34.4	99.1 102.1	100.6	6.9 7.1	7.0	7.0	4.5 4.5	4.5	4.3 4.1		4.2		
M5	Sunny	Moderate	15:55	Surface	1	23.0 23.0	23.0	8.2 8.2	8.2	33.9 33.9	33.9	106.3 104.9	105.6	7.4 7.3	7.4	7.2	7.2	2.2 2.2	2.2	3.1	5.1 5.1	5.1	5.5
				Middle	5.5	22.6 22.6	22.6	8.3 8.3	8.3	34.4 34.4	34.4	99.7 99.0	99.4	6.9 6.9	6.9	6.9	2.3 2.4	2.4	8.6 8.2		8.4		
				Bottom	10	21.0 20.9	21.0	8.1 8.1	8.1	34.3 34.3	34.3	88.9 89.3	89.1	6.2 6.2	6.2	6.2	4.5 4.9	4.7	3.1 3.1		3.1		
M6	Sunny	Moderate	15:44	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	2.1	-	-	6.5
				Middle	2.1	22.4 22.4	22.4	8.2 8.2	8.2	34.0 34.0	34.0	106.2 106.7	106.5	7.3 7.4	7.4	7.4	2.1 2.0	2.1	6.6 6.4		6.5		
				Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-	-	

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 4 April 2018 (Mid-Flood Tide)

<u>Parameter</u> <u>(unit)</u>	<u>Depth</u>	<u>Action Level</u>	<u>Limit Level</u>
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 5.5 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 6.0 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.0 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.5 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.0 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.5 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.1 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u>
<u>Station M6</u>			
Intake Level		<u>8.3 mg/L</u>	<u>8.6 mg/L</u>

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 04 April 2018

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity (NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Sunny	Moderate	09:46	Surface	1	23.3 23.5	23.4	8.2 8.2	8.2	33.5 33.5	33.5	113.8 112.0	112.9	7.9 7.8	7.9	7.4	2.2 2.3	2.3	3.0	5.0 4.9	5.0	4.9
				Middle	9	22.3 22.1	22.2	8.2 8.2	8.2	34.6 33.8	34.2	97.1 97.2	97.2	6.8 6.8	6.8		2.2 2.2	2.2		4.6 4.5	4.6	
				Bottom	17	19.2 19.3	19.3	8.1 8.1	8.1	37.5 34.5	36.0	86.9 87.8	87.4	6.1 6.1	6.1		4.4 4.7	4.6		5.1 5.1	5.1	
C2	Sunny	Moderate	08:20	Surface	1	22.8 22.8	22.8	8.2 8.3	8.3	33.4 33.5	33.5	103.8 102.6	103.2	7.3 7.2	7.3	6.9	2.3 2.3	2.3	3.4	4.1 4.2	4.2	3.1
				Middle	16.5	21.9 21.8	21.9	8.2 8.2	8.2	33.9 34.0	34.0	89.5 92.1	90.8	6.3 6.5	6.4		3.3 3.4	3.4		2.3 2.2	2.3	
				Bottom	32	20.5 20.3	20.4	8.2 8.2	8.2	33.9 34.1	34.0	81.8 82.6	82.2	5.8 5.8	5.8		4.6 4.5	4.6		2.9 2.8	2.9	
G1	Sunny	Moderate	09:04	Surface	1	22.7 22.7	22.7	8.3 8.3	8.3	33.6 33.6	33.6	114.4 110.5	112.5	7.9 7.7	7.8	7.8	2.3 2.3	2.3	3.2	4.0 4.0	4.0	4.1
				Middle	4	22.3 22.2	22.3	8.2 8.2	8.2	34.1 34.1	34.1	112.4 111.0	111.7	7.8 7.7	7.8		2.5 2.7	2.6		2.3 2.3	2.3	
				Bottom	7	21.5 21.6	21.6	8.2 8.2	8.2	34.4 34.3	34.4	100.2 99.1	99.7	7.0 6.9	7.0		4.5 4.6	4.6		6.1 5.8	6.0	
G2	Sunny	Moderate	08:50	Surface	1	22.6 22.6	22.6	8.3 8.3	8.3	33.6 33.6	33.6	116.4 115.6	116.0	8.1 8.0	8.1	7.7	2.3 2.2	2.3	2.8	3.0 3.0	3.0	3.8
				Middle	5	22.1 22.1	22.1	8.2 8.2	8.2	34.2 34.3	34.3	103.3 102.7	103.0	7.2 7.2	7.2		2.8 2.8	2.8		3.4 3.4	3.4	
				Bottom	9	21.4 21.4	21.4	8.2 8.2	8.2	34.5 34.6	34.6	91.4 94.3	92.9	6.4 6.6	6.5		3.3 3.4	3.4		5.1 5.1	5.1	
G3	Sunny	Moderate	09:13	Surface	1	22.9 23.0	23.0	8.3 8.3	8.3	33.1 33.0	33.1	105.6 91.2	98.4	7.4 6.4	6.9	7.0	2.4 2.4	2.4	2.8	4.5 4.6	4.6	4.3
				Middle	4	22.3 22.3	22.3	8.2 8.3	8.3	33.9 33.9	33.9	101.0 101.7	101.1	7.0 7.0	7.0		2.8 2.8	2.8		4.4 4.5	4.5	
				Bottom	7	22.0 22.0	22.0	8.2 8.2	8.2	34.4 34.4	34.4	92.3 94.0	93.2	6.5 6.6	6.6		3.2 3.1	3.2		3.6 3.8	3.7	
G4	Sunny	Moderate	09:25	Surface	1	23.3 22.7	23.0	8.3 8.3	8.3	33.2 33.6	33.4	113.4 111.9	112.7	7.8 7.8	7.8	7.8	2.4 2.3	2.4	3.2	4.3 4.2	4.3	4.5
				Middle	4.5	22.3 22.3	22.3	8.2 8.2	8.2	34.1 34.1	34.1	110.4 110.3	110.4	7.7 7.7	7.7		2.4 2.5	2.5		3.2 3.2	3.2	
				Bottom	8	21.6 21.6	21.6	8.2 8.2	8.2	34.3 34.3	34.3	91.8 92.5	92.2	6.4 6.5	6.5		4.6 4.7	4.7		6.1 6.1	6.1	
M1	Sunny	Moderate	08:58	Surface	1	22.7 22.7	22.7	8.3 8.3	8.3	33.6 33.6	33.6	114.5 109.2	111.9	7.9 7.6	7.8	7.7	2.3 2.4	2.4	2.6	3.6 3.7	3.7	4.1
				Middle	3	22.3 22.4	22.4	8.2 8.2	8.2	33.9 33.9	33.9	109.9 110.2	110.1	7.6 7.6	7.6		2.6 2.6	2.6		5.1 5.0	5.1	
				Bottom	5	22.1 22.2	22.2	8.2 8.2	8.2	34.3 34.2	34.3	99.6 99.1	99.4	6.9 6.9	6.9		2.6 2.8	2.7		3.5 3.5	3.5	
M2	Sunny	Moderate	08:42	Surface	1	22.6 22.7	22.7	8.3 8.3	8.3	33.6 33.6	33.6	116.0 114.0	115.0	8.1 7.9	8.0	7.6	2.4 2.3	2.4	3.6	4.6 4.9	4.8	4.0
				Middle	5.5	21.8 21.7	21.8	8.2 8.2	8.2	35.0 34.1	34.6	102.5 105.1	103.8	7.1 7.3	7.2		4.1 4.1	4.1		3.0 3.0	3.0	
				Bottom	10	21.3 21.2	21.3	8.1 8.1	8.1	34.5 34.6	34.6	84.7 88.8	86.8	5.9 6.2	6.1		4.2 4.5	4.4		4.2 4.3	4.3	
M3	Sunny	Moderate	09:18	Surface	1	23.0 22.9	23.0	8.2 8.2	8.2	33.2 33.3	33.3	99.5 96.9	98.2	6.9 6.8	6.9	6.9	2.3 2.4	2.4	3.0	2.6 2.5	2.6	3.9
				Middle	4	22.2 22.3	22.3	8.2 8.2	8.2	34.0 34.1	34.1	96.1 102.2	99.2	6.7 7.1	6.9		2.9 2.9	2.9		4.1 4.0	4.1	
				Bottom	7	21.9 22.0	22.0	8.2 8.3	8.3	34.6 34.5	34.6	94.1 93.3	93.7	6.6 6.5	6.6		3.6 3.7	3.7		5.0 5.1	5.1	
M4	Sunny	Moderate	08:29	Surface	1	22.7 22.8	22.8	8.3 8.3	8.3	33.5 33.5	33.5	111.3 109.8	110.6	7.8 7.7	7.8	7.2	2.3 2.3	2.3	2.5	5.5 5.4	5.5	4.0
				Middle	5	22.6 22.4	22.5	8.3 8.2	8.3	33.6 33.9	33.8	90.3 94.9	92.6	6.3 6.6	6.5		2.4 2.5	2.5		3.1 3.1	3.1	
				Bottom	9	22.5 22.3	22.4	8.2 8.2	8.2	33.8 34.1	34.0	84.3 86.7	85.5	5.9 6.1	6.0		2.4 2.7	2.6		3.5 3.3	3.4	
M5	Sunny	Moderate	09:37	Surface	1	22.7 22.9	22.8	8.3 8.3	8.3	33.6 33.6	33.6	112.0 111.0	111.5	7.8 7.7	7.8	7.7	2.6 2.3	2.5	3.1	4.5 4.4	4.5	5.4
				Middle	5.5	22.5 22.5	22.5	8.2 8.2	8.2	33.9 33.8	33.9	108.9 107.0	108.0	7.6 7.4	7.5		2.4 2.3	2.4		8.4 8.5	8.5	
				Bottom	10	21.8 21.7	21.8	8.2 8.2	8.2	33.9 34.0	34.0	109.3 108.0	108.7	7.6 7.5	7.6		4.4 4.3	4.4		3.1 3.0	3.1	
M6	Sunny	Moderate	09:31	Surface	-	-	-	-	-	-	-	-	-	-	6.6	-	-	2.3	-	-	3.5	
				Middle	1.6	22.6 22.6	22.6	8.2 8.3	8.3	33.7 33.7	33.7	94.1 93.8	94.0	6.6 6.5		6.6	2.3 2.3		2.3	3.4 3.5		3.5
				Bottom	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 6 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.4 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.6 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.7 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.3 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.7 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.3 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.8 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 8.5 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 06 April 2018

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Sunny	Calm	16:41	Surface	1	22.5 22.6	22.6	8.0 8.0	8.0	33.2 32.9	33.1	97.9 97.0	97.5	7.0 6.9	7.0	6.9	1.1 1.1	1.1	1.7	5.0 6.2	5.6	5.8
				Middle	10	22.5 22.3	22.4	8.0 8.0	8.0	33.2 33.4	33.3	96.4 94.1	95.3	6.9 6.7	6.8		2.0 2.0	2.0		4.8 4.9	4.9	
				Bottom	19	22.3 22.3	22.3	8.0 8.0	8.0	33.4 33.4	33.4	94.5 94.0	94.3	6.8 6.7	6.8		2.0 1.9	2.0		6.9 6.7	6.8	
C2	Sunny	Calm	14:40	Surface	1	22.8 22.8	22.8	7.9 7.9	7.9	32.4 32.5	32.5	92.8 92.8	92.8	6.6 6.6	6.6	6.7	1.0 1.1	1.1	2.1	5.0 6.1	5.6	5.0
				Middle	17	22.3 22.3	22.3	8.0 8.0	8.0	33.5 33.5	33.5	93.2 93.3	93.3	6.7 6.7	6.7		2.3 2.4	2.4		2.8 2.7	2.8	
				Bottom	33	22.2 22.2	22.2	8.0 8.0	8.0	33.6 33.6	33.6	92.5 92.6	92.6	6.6 6.6	6.6		2.8 2.8	2.8		6.4 6.5	6.5	
G1	Sunny	Calm	15:40	Surface	1	23.0 23.0	23.0	8.0 8.0	8.0	33.0 33.0	33.0	102.0 102.0	102.0	7.2 7.2	7.2	7.1	0.8 0.7	0.8	1.5	4.2 4.3	4.3	4.5
				Middle	4	22.7 22.6	22.7	8.0 8.0	8.0	33.2 33.2	33.2	98.5 98.5	98.5	7.0 7.0	7.0		1.4 1.4	1.4		5.7 5.8	5.8	
				Bottom	7	22.3 22.3	22.3	8.0 8.0	8.0	33.5 33.5	33.5	96.7 96.5	96.6	6.9 6.9	6.9		2.4 2.4	2.4		3.3 3.2	3.3	
G2	Sunny	Calm	15:20	Surface	1	23.1 23.1	23.1	8.0 8.0	8.0	32.9 32.9	32.9	103.7 103.4	103.6	7.4 7.3	7.4	7.3	0.7 0.7	0.7	1.0	3.0 3.1	3.1	4.2
				Middle	5	22.5 22.5	22.5	8.0 8.0	8.0	33.2 33.3	33.3	99.1 98.7	98.9	7.1 7.1	7.1		0.9 1.0	1.0		4.0 4.1	4.1	
				Bottom	9	22.3 22.3	22.3	8.0 8.0	8.0	33.5 33.5	33.5	96.6 96.4	96.5	6.9 6.9	6.9		1.2 1.4	1.3		5.1 5.5	5.4	
G3	Sunny	Calm	15:52	Surface	1	22.5 22.5	22.5	8.0 8.0	8.0	32.6 32.6	32.6	96.8 96.3	96.6	6.9 6.9	6.9	6.9	2.0 2.0	2.0	2.7	5.5 5.5	5.5	4.1
				Middle	4	22.4 22.4	22.4	8.0 8.0	8.0	33.4 33.4	33.4	94.8 94.9	94.9	6.8 6.8	6.8		2.9 2.8	2.9		3.7 3.6	3.7	
				Bottom	7	22.2 22.2	22.2	8.0 8.0	8.0	33.7 33.7	33.7	94.4 94.4	94.4	6.8 6.8	6.8		3.2 3.2	3.2		3.0 3.1	3.1	
G4	Sunny	Calm	16:14	Surface	1	22.5 22.5	22.5	8.0 8.0	8.0	33.2 33.2	33.2	100.6 100.9	100.8	7.2 7.2	7.2	7.2	1.4 1.4	1.4	1.4	5.9 5.8	5.9	6.3
				Middle	4	22.4 22.5	22.5	8.0 8.0	8.0	33.4 33.3	33.4	99.8 100.1	100.0	7.1 7.2	7.2		1.1 1.2	1.2		6.2 6.3	6.3	
				Bottom	7	22.2 22.2	22.2	8.1 8.0	8.1	33.7 33.7	33.7	98.5 97.9	98.1	7.0 7.0	7.0		1.6 1.8	1.7		6.7 6.6	6.7	
M1	Sunny	Calm	15:31	Surface	1	23.1 23.0	23.1	8.0 8.0	8.0	33.0 33.0	33.0	102.1 101.1	101.6	7.2 7.2	7.2	7.1	0.8 0.9	0.9	1.2	2.8 2.8	2.8	3.9
				Middle	3	22.7 22.7	22.7	8.0 8.0	8.0	33.2 33.2	33.2	98.8 98.7	98.8	7.0 7.0	7.0		1.2 1.1	1.2		4.7 4.7	4.7	
				Bottom	5	22.5 22.5	22.5	8.0 8.0	8.0	33.3 33.3	33.3	97.8 97.7	97.8	7.0 7.0	7.0		1.5 1.6	1.6		4.2 4.3	4.3	
M2	Sunny	Calm	15:10	Surface	1	23.1 23.1	23.1	8.0 8.0	8.0	32.9 32.9	32.9	103.5 103.1	103.3	7.3 7.3	7.3	7.1	0.6 0.6	0.6	1.2	4.6 4.7	4.7	5.0
				Middle	5.5	22.4 22.4	22.4	8.0 8.0	8.0	33.4 33.4	33.4	95.8 95.9	95.9	6.9 6.9	6.9		1.4 1.4	1.4		5.8 5.7	5.8	
				Bottom	10	22.2 22.2	22.2	8.0 8.0	8.0	33.7 33.7	33.7	95.9 95.8	95.9	6.9 6.9	6.9		1.4 1.6	1.5		4.4 4.5	4.5	
M3	Sunny	Calm	16:02	Surface	1	22.6 22.6	22.6	8.0 8.0	8.0	33.0 33.0	33.0	91.9 92.3	92.1	6.6 6.6	6.6	6.7	2.9 2.8	2.9	2.9	5.5 5.6	5.6	6.1
				Middle	4	22.4 22.4	22.4	8.0 8.0	8.0	33.4 33.4	33.4	95.4 94.9	95.2	6.8 6.8	6.8		2.6 2.7	2.7		6.1 6.0	6.1	
				Bottom	7	22.2 22.2	22.2	8.0 8.0	8.0	33.7 33.7	33.7	93.9 94.1	94.0	6.7 6.7	6.7		3.0 2.9	3.0		6.5 6.5	6.5	
M4	Sunny	Calm	14:55	Surface	1	22.9 22.8	22.9	8.0 8.0	8.0	33.0 33.1	33.1	101.3 100.1	100.7	7.2 7.1	7.2	7.1	0.9 1.0	1.0	1.6	3.7 3.5	3.6	4.4
				Middle	5	22.6 22.6	22.6	8.0 8.0	8.0	33.2 33.2	33.2	97.0 97.0	97.0	6.9 6.9	6.9		1.4 1.5	1.5		3.5 3.6	3.6	
				Bottom	9	22.4 22.4	22.4	8.0 8.0	8.0	33.4 33.4	33.4	94.1 93.8	94.0	6.7 6.7	6.7		2.2 2.2	2.2		5.9 5.9	5.9	
M5	Sunny	Calm	16:31	Surface	1	22.5 22.5	22.5	8.0 8.0	8.0	33.1 33.1	33.1	101.2 101.2	101.2	7.2 7.2	7.2	7.2	0.8 0.8	0.8	0.9	3.0 3.0	3.0	4.0
				Middle	5	22.6 22.6	22.6	8.0 8.0	8.0	33.1 33.1	33.1	100.4 100.4	100.4	7.2 7.2	7.2		1.0 0.8	0.9		5.7 5.7	5.7	
				Bottom	9	22.4 22.4	22.4	8.0 8.0	8.0	33.4 33.4	33.4	97.5 97.4	97.5	7.0 7.0	7.0		1.1 1.1	1.1		3.2 3.2	3.2	
M6	Sunny	Calm	16:24	Surface	-	-	-	-	-	-	-	-	-	-	-	7.0	-	-	2.2	-	-	6.9
				Middle	2.1	22.4 22.4	22.4	8.0 8.0	8.0	33.4 33.4	33.4	97.8 97.6	97.7	7.0 7.0	7.0		2.2 2.1	2.2		6.9 6.8	6.9	
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-	

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 6 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 3.1 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 3.4 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.8 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.4 mg/L</u>
<u>Station M6</u>			
Intake Level		<u>8.3 mg/L</u>	<u>8.6 mg/L</u>

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 06 April 2018

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Sunny	Calm	10:42	Surface	1	23.0 23.0	23.0	8.0 8.0	8.0	32.8 32.8	32.8	95.0 95.2	95.1	6.7 6.8	6.8	6.9	0.7 0.8	0.8	1.4	4.8 4.9	4.9	4.9
				Middle	9.5	22.5 22.5	22.5	8.0 8.0	8.0	33.2 33.2	33.2	96.9 97.2	97.1	6.9 6.9	6.9		0.7 0.8	0.8		4.2 4.2	4.2	
				Bottom	18	22.1 22.1	22.1	8.0 8.0	8.0	33.9 33.9	33.9	94.8 94.8	94.8	6.8 6.8	6.8		2.6 2.5	2.6		5.6 5.8	5.7	
C2	Sunny	Calm	08:31	Surface	1	22.6 22.6	22.6	8.0 8.0	8.0	32.9 32.9	32.9	94.1 94.3	94.2	6.7 6.7	6.7	6.7	0.7 0.7	0.7	1.6	4.4 4.4	4.4	4.3
				Middle	17	22.3 22.3	22.3	8.0 8.0	8.0	33.4 33.4	33.4	93.4 93.4	93.4	6.7 6.7	6.7		1.3 1.3	1.3		4.3 4.2	4.3	
				Bottom	33	22.1 22.1	22.1	8.0 8.0	8.0	33.8 33.8	33.8	93.9 94.0	94.0	6.7 6.7	6.7		2.7 2.7	2.7		4.3 4.3	4.3	
G1	Sunny	Calm	09:35	Surface	1	22.9 22.8	22.9	8.0 8.0	8.0	32.8 32.8	32.8	96.5 96.3	96.5	6.9 6.9	6.9	6.9	0.6 0.6	0.6	0.8	4.7 4.6	4.7	4.1
				Middle	4	22.7 22.7	22.7	8.0 8.0	8.0	32.9 32.9	32.9	97.2 97.4	97.3	6.9 6.9	6.9		0.7 0.6	0.7		4.2 4.2	4.2	
				Bottom	7	22.5 22.5	22.5	8.0 8.0	8.0	33.1 33.1	33.1	95.9 95.9	95.9	6.9 6.9	6.9		1.0 1.0	1.0		3.4 3.4	3.4	
G2	Sunny	Calm	09:15	Surface	1	22.8 22.7	22.8	8.0 8.0	8.0	32.8 32.8	32.8	95.8 95.9	95.9	6.9 6.9	6.9	6.9	0.6 0.6	0.6	0.7	5.5 5.6	5.6	3.9
				Middle	5	22.6 22.6	22.6	8.0 8.0	8.0	33.0 33.0	33.0	96.2 96.0	96.1	6.9 6.9	6.9		0.7 0.7	0.7		2.7 2.7	2.7	
				Bottom	9	22.5 22.4	22.5	8.0 8.0	8.0	33.2 33.2	33.2	94.9 94.9	94.9	6.8 6.8	6.8		0.8 0.8	0.8		3.4 3.5	3.5	
G3	Sunny	Calm	09:49	Surface	1	23.4 23.3	23.4	8.0 8.0	8.0	32.2 32.4	32.3	94.7 96.0	95.4	6.7 6.8	6.8	6.9	0.4 0.4	0.4	0.7	3.4 3.4	3.4	4.0
				Middle	4	22.7 22.7	22.7	8.0 8.0	8.0	33.0 33.0	33.0	97.3 97.6	97.5	7.0 7.0	7.0		0.7 0.7	0.7		3.3 3.3	3.3	
				Bottom	7	22.6 22.6	22.6	8.0 8.0	8.0	33.1 33.1	33.1	95.5 95.5	95.5	6.8 6.8	6.8		0.8 0.9	0.9		5.2 5.3	5.3	
G4	Sunny	Calm	10:10	Surface	1	22.9 22.9	22.9	8.0 8.0	8.0	32.9 32.8	32.9	97.9 97.4	97.7	7.0 6.9	7.0	7.0	0.6 0.6	0.6	0.7	4.8 5.1	5.0	5.9
				Middle	4	22.7 22.7	22.7	8.0 8.0	8.0	32.9 32.9	32.9	98.4 98.4	98.4	7.0 7.0	7.0		0.7 0.7	0.7		6.6 6.8	6.7	
				Bottom	7	22.6 22.6	22.6	8.0 8.0	8.0	33.1 33.1	33.1	97.4 97.5	97.5	7.0 7.0	7.0		0.8 0.8	0.8		5.9 5.9	5.9	
M1	Sunny	Calm	09:26	Surface	1	22.8 22.8	22.8	8.0 8.0	8.0	32.8 32.9	32.9	96.5 95.6	96.1	6.9 6.8	6.9	6.9	0.6 0.7	0.7	0.8	2.8 2.8	2.8	3.4
				Middle	3	22.8 22.8	22.8	8.0 8.0	8.0	32.9 32.9	32.9	95.3 95.2	95.3	6.8 6.8	6.8		0.8 0.8	0.8		3.3 3.3	3.3	
				Bottom	5	22.7 22.7	22.7	8.0 8.0	8.0	32.9 32.9	32.9	94.3 94.4	94.4	6.7 6.7	6.7		0.8 0.8	0.8		4.2 4.2	4.2	
M2	Sunny	Calm	09:05	Surface	1	22.7 22.7	22.7	8.0 8.0	8.0	32.9 32.9	32.9	97.0 96.7	96.9	6.9 6.9	6.9	6.9	0.7 0.7	0.7	1.2	2.1 2.1	2.1	3.3
				Middle	5.5	22.4 22.5	22.5	8.0 8.0	8.0	33.3 33.2	33.3	95.3 95.3	95.3	6.8 6.8	6.8		0.8 0.8	0.8		2.9 3.0	3.0	
				Bottom	10	22.3 22.3	22.3	8.0 8.0	8.0	33.5 33.5	33.5	94.7 94.7	94.7	6.8 6.8	6.8		2.0 2.0	2.0		4.8 4.7	4.8	
M3	Sunny	Calm	09:59	Surface	1	23.0 23.1	23.1	8.0 8.0	8.0	32.6 32.4	32.5	95.3 96.2	95.8	6.8 6.8	6.8	6.9	0.5 0.5	0.5	0.7	2.7 2.7	2.7	3.3
				Middle	4	22.8 22.8	22.8	8.0 8.0	8.0	32.9 32.9	32.9	97.7 97.3	97.5	7.0 6.9	7.0		0.6 0.7	0.7		3.5 3.4	3.5	
				Bottom	7	22.7 22.7	22.7	8.0 8.0	8.0	33.0 33.0	33.0	92.9 94.7	93.8	6.6 6.8	6.7		0.8 0.7	0.8		3.6 3.7	3.7	
M4	Sunny	Calm	08:50	Surface	1	22.9 23.0	23.0	8.0 8.0	8.0	32.8 32.8	32.8	96.0 96.1	96.1	6.8 6.8	6.8	6.8	0.5 0.5	0.5	1.1	5.3 5.4	5.4	3.9
				Middle	5	22.5 22.5	22.5	8.0 8.0	8.0	33.2 33.2	33.2	95.2 95.5	95.4	6.8 6.8	6.8		0.8 0.9	0.9		2.1 2.1	2.1	
				Bottom	9	22.3 22.3	22.3	8.0 8.0	8.0	33.5 33.5	33.5	95.3 95.4	95.4	6.8 6.8	6.8		1.8 2.1	2.0		4.2 4.2	4.2	
M5	Sunny	Calm	10:28	Surface	1	22.9 23.1	23.0	8.0 8.0	8.0	32.8 32.8	32.8	95.0 94.8	94.9	6.8 6.7	6.8	6.8	0.7 0.7	0.7	1.1	5.1 5.2	5.2	4.6
				Middle	5	22.6 22.4	22.5	8.0 8.0	8.0	33.0 33.2	33.1	95.6 95.4	95.5	6.8 6.8	6.8		1.0 1.2	1.1		2.6 2.6	2.6	
				Bottom	9	22.3 22.3	22.3	8.0 8.0	8.0	33.4 33.5	33.5	94.9 95.0	95.0	6.8 6.8	6.8		1.5 1.7	1.6		5.9 6.1	6.0	
M6	Sunny	Calm	10:21	Surface	-	-	-	-	-	-	-	-	-	-	7.0	-	-	0.9	-	-	3.4	
				Middle	2.1	22.7 22.7	22.7	8.0 8.0	8.0	33.0 33.0	33.0	97.9 97.8	97.9	7.0 7.0		7.0	0.8 0.9		0.9	3.4 3.4		3.4
				Bottom	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 10 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 2.6 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 2.9 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.1 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.1mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 8.0 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 8.7 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 10 April 2018

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition*	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Sunny	Calm	20:18	Surface	1	22.8 22.7	22.8	8.5 8.5	8.5	33.6 33.6	33.6	123.7 122.0	122.9	8.8 8.7	8.8	8.3	0.5 0.4	0.5	0.8	4.1 4.1	4.1	5.2
				Middle	9	22.1 22.0	22.1	8.4 8.4	8.4	33.6 33.6	33.6	106.3 107.3	106.8	7.6 7.7	7.7		0.6 0.6	0.6		5.2 5.3	5.3	
				Bottom	17	22.0 22.0	22.0	8.4 8.4	8.4	33.6 33.6	33.6	102.7 103.4	103.1	7.4 7.4	7.4		1.3 1.1	1.2		6.2 6.1	6.2	
C2	Sunny	Calm	19:15	Surface	1	22.2 22.2	22.2	8.4 8.4	8.4	33.5 33.5	33.5	98.0 100.8	99.4	7.0 7.2	7.1	7.1	2.2 2.1	2.2	2.1	5.2 5.0	5.1	5.6
				Middle	16.5	22.1 22.1	22.1	8.4 8.4	8.4	33.5 33.6	33.6	98.5 98.5	98.5	7.1 7.1	7.1		2.0 2.0	2.0		5.1 5.1	5.1	
				Bottom	32	21.9 22.0	22.0	8.4 8.4	8.4	33.6 33.6	33.6	94.6 95.4	95.0	6.8 6.9	6.9		2.2 2.2	2.2		6.6 6.8	6.7	
G1	Sunny	Calm	19:42	Surface	1	23.3 23.4	23.4	8.5 8.5	8.5	33.5 33.5	33.5	129.3 132.0	130.7	9.1 9.3	9.2	9.1	0.7 0.8	0.8	0.8	5.4 5.3	5.4	5.6
				Middle	4	23.0 23.0	23.0	8.5 8.5	8.5	33.5 33.5	33.5	125.2 125.3	125.3	8.9 8.9	8.9		0.6 0.7	0.7		6.5 6.5	6.5	
				Bottom	7	22.7 22.7	22.7	8.5 8.5	8.5	33.5 33.5	33.5	124.5 124.3	124.4	8.9 8.8	8.9		0.9 0.9	0.9		4.8 5.0	4.9	
G2	Sunny	Calm	19:33	Surface	1	23.0 23.0	23.0	8.5 8.5	8.5	33.5 33.5	33.5	118.7 122.7	120.7	8.4 8.7	8.6	8.8	0.7 0.7	0.7	0.8	5.4 5.3	5.4	5.2
				Middle	5	22.4 22.4	22.4	8.5 8.5	8.5	33.5 33.5	33.5	123.1 123.9	123.5	8.8 8.9	8.9		0.7 0.7	0.7		4.9 4.7	4.8	
				Bottom	9	22.0 22.0	22.0	8.5 8.5	8.5	33.6 33.6	33.6	117.4 115.0	116.2	8.4 8.3	8.4		0.9 0.9	0.9		5.3 5.2	5.3	
G3	Sunny	Calm	19:47	Surface	1	23.6 23.5	23.6	8.5 8.5	8.5	33.5 33.5	33.5	134.8 135.8	135.3	9.4 9.5	9.5	9.6	0.6 0.7	0.7	0.9	5.7 6.0	5.9	5.3
				Middle	4	23.1 23.1	23.1	8.5 8.5	8.5	33.5 33.5	33.5	135.5 135.4	135.5	9.6 9.6	9.6		0.8 1.0	0.9		6.9 6.7	6.8	
				Bottom	7	22.5 22.5	22.5	8.5 8.5	8.5	33.5 33.5	33.5	133.3 128.5	130.9	9.5 9.2	9.4		1.0 1.2	1.1		3.1 3.0	3.1	
G4	Sunny	Calm	19:59	Surface	1	23.5 23.5	23.5	8.5 8.5	8.5	33.5 33.5	33.5	134.3 135.0	134.7	9.4 9.5	9.5	9.4	0.7 0.6	0.7	1.3	4.7 4.6	4.7	5.6
				Middle	4.5	23.0 23.1	23.1	8.5 8.5	8.5	33.5 33.5	33.5	129.4 129.1	129.3	9.2 9.1	9.2		0.8 0.7	0.8		5.7 5.5	5.6	
				Bottom	8	22.1 22.4	22.3	8.5 8.5	8.5	33.6 33.6	33.6	124.2 128.9	126.6	8.9 9.2	9.1		2.3 2.4	2.4		6.3 6.7	6.5	
M1	Sunny	Calm	19:38	Surface	1	23.3 23.3	23.3	8.5 8.5	8.5	33.5 33.5	33.5	128.3 129.0	128.7	9.0 9.1	9.1	9.0	0.7 0.8	0.8	0.8	4.0 4.0	4.0	4.2
				Middle	3	23.1 23.0	23.1	8.5 8.5	8.5	33.5 33.5	33.5	125.9 125.1	125.5	8.9 8.8	8.9		0.6 0.7	0.7		3.8 3.7	3.8	
				Bottom	5	22.9 22.9	22.9	8.5 8.5	8.5	33.5 33.5	33.5	122.3 123.4	122.9	8.7 8.7	8.7		0.8 0.7	0.8		4.8 4.9	4.9	
M2	Sunny	Calm	19:28	Surface	1	22.9 22.9	22.9	8.5 8.5	8.5	33.5 33.5	33.5	121.6 121.3	121.5	8.6 8.6	8.6	8.1	0.4 0.5	0.5	1.0	5.3 5.3	5.3	5.4
				Middle	6	22.0 22.0	22.0	8.4 8.4	8.4	33.6 33.6	33.6	103.6 104.3	104.0	7.5 7.5	7.5		1.1 1.0	1.1		5.8 5.6	5.7	
				Bottom	11	21.9 21.9	21.9	8.4 8.4	8.4	33.6 33.6	33.6	101.8 105.0	103.4	7.3 7.6	7.5		1.4 1.2	1.3		5.1 5.0	5.1	
M3	Sunny	Calm	19:53	Surface	1	23.5 23.3	23.4	8.5 8.5	8.5	33.5 33.5	33.5	133.6 136.2	134.9	9.4 9.6	9.5	9.6	0.6 0.6	0.6	1.1	4.3 4.4	4.4	5.3
				Middle	4	23.0 23.0	23.0	8.5 8.5	8.5	33.5 33.5	33.5	134.6 135.3	135.0	9.5 9.6	9.6		0.8 0.8	0.8		7.7 7.6	7.7	
				Bottom	7	22.5 22.2	22.4	8.5 8.5	8.5	33.5 33.5	33.5	131.2 120.3	125.8	9.4 8.6	9.0		2.0 1.9	2.0		3.8 3.8	3.8	
M4	Sunny	Calm	19:22	Surface	1	22.3 22.3	22.3	8.4 8.4	8.4	33.5 33.5	33.5	103.7 104.4	104.1	7.4 7.5	7.5	7.4	1.3 1.1	1.2	1.5	4.2 4.0	4.1	4.2
				Middle	5	22.2 22.0	22.1	8.4 8.4	8.4	33.6 33.6	33.6	100.9 98.7	99.8	7.2 7.1	7.2		1.4 1.4	1.4		2.9 3.0	3.0	
				Bottom	9	22.0 21.9	22.0	8.4 8.4	8.4	33.6 33.6	33.6	98.0 97.0	97.5	7.1 7.0	7.1		1.9 2.0	2.0		5.6 5.6	5.6	
M5	Sunny	Calm	20:11	Surface	1	22.7 22.7	22.7	8.5 8.5	8.5	33.5 33.6	33.6	125.0 126.1	125.6	8.9 9.0	9.0	9.0	0.8 0.8	0.8	0.9	5.6 5.6	5.6	5.7
				Middle	5.5	22.6 22.6	22.6	8.5 8.5	8.5	33.5 33.5	33.5	126.3 126.5	126.4	9.0 9.0	9.0		0.7 0.8	0.8		6.1 6.0	6.1	
				Bottom	10	22.4 22.4	22.4	8.5 8.5	8.5	33.6 33.6	33.6	124.9 123.9	124.4	8.9 8.9	8.9		1.0 1.1	1.1		5.5 5.5	5.5	
M6	Sunny	Calm	20:03	Surface	-	-	-	-	-	-	-	-	-	-	-	9.4	-	-	0.7	-	-	5.8
				Middle	1.1	23.3 23.3	23.3	8.5 8.5	8.5	33.5 33.5	33.5	131.8 134.7	133.3	9.3 9.5	9.4		0.7 0.7	0.7		5.9 5.7	5.8	
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-	

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 10 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 4.9 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 5.3 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.0 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.5 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.0 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.5 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.7 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.3 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 10 April 2018**

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Sunny	Calm	14:11	Surface	1	22.3 22.8	22.6	8.5 8.5	8.5	33.5 33.5	33.5	115.1 115.3	115.2	8.2 8.2	8.2	8.0	1.0 1.0	1.0	2.2	5.8 5.7	5.8	5.7
				Middle	9	22.0 22.2	22.1	8.4 8.5	8.5	33.7 33.6	33.7	101.8 112.6	107.2	7.3 8.1	7.7		1.5 1.4	1.5		5.7 5.5	5.6	
				Bottom	17	21.9 21.9	21.9	8.4 8.4	8.4	33.7 33.7	33.7	97.8 99.2	98.5	7.0 7.1	7.1		4.0 4.1	4.1		5.6 5.6	5.6	
C2	Sunny	Calm	13:15	Surface	1	22.7 22.5	22.6	8.3 8.4	8.4	33.4 33.4	33.4	106.8 105.9	106.4	7.6 7.6	7.6	7.3	0.9 0.9	0.9	1.1	5.9 5.7	5.8	4.6
				Middle	16.5	22.0 22.0	22.0	8.4 8.4	8.4	33.6 33.6	33.6	96.9 97.1	97.0	7.0 7.0	7.0		1.3 1.2	1.3		5.0 5.0	5.0	
				Bottom	32	22.0 22.0	22.0	8.4 8.4	8.4	33.6 33.6	33.6	97.6 96.7	97.2	7.0 7.0	7.0		1.2 1.2	1.2		2.9 2.8	2.9	
G1	Sunny	Calm	13:40	Surface	1	23.3 23.4	23.4	8.5 8.5	8.5	33.5 33.5	33.5	127.5 128.5	128.0	9.0 9.0	9.0	9.0	0.7 0.7	0.7	0.9	4.5 4.5	4.5	5.4
				Middle	4	22.3 22.5	22.4	8.5 8.5	8.5	33.5 33.5	33.5	124.4 127.2	125.8	8.9 9.1	9.0		0.9 0.8	0.9		5.4 5.7	5.6	
				Bottom	7	22.0 22.0	22.0	8.5 8.5	8.5	33.6 33.6	33.6	117.0 119.0	118.0	8.4 8.6	8.5		1.1 1.0	1.1		5.9 6.2	6.1	
G2	Sunny	Calm	13:31	Surface	1	23.1 23.1	23.1	8.5 8.5	8.5	33.5 33.5	33.5	120.9 121.3	121.1	8.6 8.6	8.6	8.8	0.7 0.8	0.8	1.0	4.9 5.0	5.0	5.1
				Middle	5	22.2 22.3	22.3	8.5 8.5	8.5	33.6 33.5	33.6	123.5 122.9	123.2	8.9 8.8	8.9		0.7 0.8	0.8		5.1 5.1	5.1	
				Bottom	9	21.9 21.9	21.9	8.4 8.4	8.4	33.6 33.6	33.6	107.8 109.0	108.4	7.8 7.9	7.9		1.3 1.4	1.4		5.1 5.1	5.1	
G3	Sunny	Calm	13:44	Surface	1	22.7 22.8	22.8	8.5 8.5	8.5	33.4 33.5	33.5	122.0 126.9	124.5	8.7 9.0	8.9	8.9	0.9 0.8	0.9	1.1	5.5 5.4	5.5	6.9
				Middle	3.5	22.3 22.3	22.3	8.5 8.5	8.5	33.5 33.5	33.5	122.9 124.1	123.5	8.8 8.9	8.9		1.3 1.2	1.3		8.7 8.7	8.7	
				Bottom	6	22.0 22.0	22.0	8.5 8.5	8.5	33.6 33.6	33.6	118.7 120.6	119.7	8.5 8.7	8.6		1.2 1.1	1.2		6.3 6.4	6.4	
G4	Sunny	Calm	13:53	Surface	1	22.7 22.9	22.8	8.5 8.5	8.5	33.5 33.5	33.5	128.3 130.1	129.2	9.1 9.2	9.2	9.2	1.0 0.9	1.0	2.1	5.5 5.7	5.6	5.4
				Middle	4.5	22.3 22.1	22.2	8.5 8.5	8.5	33.6 33.6	33.6	130.5 127.1	128.8	9.3 9.1	9.2		1.1 1.0	1.1		4.7 4.8	4.8	
				Bottom	8	21.9 21.9	21.9	8.4 8.4	8.4	33.6 33.6	33.6	110.4 95.4	102.9	8.0 6.9	7.5		4.1 4.2	4.2		5.6 5.7	5.7	
M1	Sunny	Calm	13:35	Surface	1	23.6 23.7	23.7	8.4 8.5	8.5	33.5 33.5	33.5	123.1 129.1	126.1	8.6 9.0	8.8	8.8	0.6 0.7	0.7	1.1	4.4 4.3	4.4	4.8
				Middle	3	23.0 22.9	23.0	8.5 8.5	8.5	33.5 33.5	33.5	122.5 124.3	123.4	8.7 8.8	8.8		0.8 0.8	0.8		4.6 4.6	4.6	
				Bottom	5	22.2 22.1	22.2	8.4 8.5	8.5	33.5 33.6	33.6	116.2 116.5	116.4	8.3 8.4	8.4		1.6 1.9	1.8		5.5 5.3	5.4	
M2	Sunny	Calm	13:27	Surface	1	23.0 23.0	23.0	8.4 8.4	8.4	33.5 33.5	33.5	114.6 117.3	116.0	8.1 8.3	8.2	8.6	0.5 0.5	0.5	1.1	5.5 5.4	5.5	5.7
				Middle	6	22.3 22.2	22.3	8.5 8.5	8.5	33.5 33.6	33.6	125.2 125.3	125.3	9.0 9.0	9.0		0.6 0.6	0.6		8.4 8.4	8.5	
				Bottom	11	21.9 21.8	21.9	8.4 8.4	8.4	33.6 33.6	33.6	97.4 99.1	98.3	7.0 7.2	7.1		2.0 2.4	2.2		3.2 3.1	3.2	
M3	Sunny	Calm	13:47	Surface	1	23.6 23.3	23.5	8.5 8.5	8.5	33.5 33.5	33.5	124.3 126.5	125.4	8.7 8.9	8.8	9.2	1.1 1.1	1.1	1.3	5.2 5.2	5.2	5.7
				Middle	3.5	22.3 22.3	22.3	8.5 8.5	8.5	33.5 33.5	33.5	131.7 132.6	132.2	9.4 9.5	9.5		1.2 1.3	1.3		5.6 5.6	5.6	
				Bottom	6	22.0 22.1	22.1	8.5 8.5	8.5	33.6 33.6	33.6	124.2 126.2	125.2	8.9 9.1	9.0		1.4 1.5	1.5		6.2 6.2	6.2	
M4	Sunny	Calm	13:22	Surface	1	22.8 22.7	22.8	8.4 8.4	8.4	33.5 33.5	33.5	106.3 108.7	107.5	7.6 7.7	7.7	7.7	0.8 0.8	0.8	1.2	4.3 4.3	4.3	5.4
				Middle	5	22.1 22.2	22.2	8.4 8.4	8.4	33.6 33.6	33.6	104.9 109.9	107.4	7.5 7.9	7.7		1.2 1.0	1.1		5.9 5.9	5.9	
				Bottom	9	22.0 22.1	22.1	8.4 8.4	8.4	33.6 33.6	33.6	100.7 102.9	101.8	7.2 7.4	7.3		2.0 1.6	1.8		6.0 5.9	6.0	
M5	Sunny	Calm	14:04	Surface	1	22.5 22.6	22.6	8.4 8.4	8.4	33.6 33.6	33.6	111.9 113.2	112.6	8.0 8.1	8.1	8.0	1.4 1.2	1.3	1.4	4.5 5.0	4.8	5.3
				Middle	5.5	22.1 22.1	22.1	8.4 8.4	8.4	33.6 33.6	33.6	109.1 109.9	109.5	7.8 7.9	7.9		1.2 1.3	1.3		5.7 5.9	5.8	
				Bottom	10	22.0 22.0	22.0	8.4 8.4	8.4	33.6 33.6	33.6	105.3 105.1	105.2	7.6 7.6	7.6		1.4 1.5	1.5		5.3 5.4	5.4	
M6	Sunny	Calm	13:58	Surface	-	-	-	-	-	-	-	-	-	-	8.4	-	-	0.7	-	-	8.0	
				Middle	1.1	23.0 22.2	22.6	8.4 8.5	8.5	33.5 33.5	33.5	113.0 121.5	117.3	8.0 8.7		8.4	0.7 0.7		0.7	8.0 8.0		8.0
				Bottom	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 12 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.1 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.4 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.0 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.5mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.0 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.5 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.6 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 8.2 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 12 April 2018

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity (NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Sunny	Calm	10:44	Surface	1	23.0 22.9	23.0	8.4 8.4	8.4	33.3 33.3	33.3	109.1 108.0	108.6	7.7 7.7	7.7	7.5	0.6 0.6	0.6	1.5	5.4 5.3	5.4	4.4
				Middle	9.5	22.5 22.4	22.5	8.4 8.4	8.4	33.5 33.6	33.6	102.1 101.3	101.7	7.3 7.2	7.3	7.0	1.0 1.0	1.0	1.0	4.1 4.0	4.1	
				Bottom	18	22.1 22.1	22.1	8.4 8.4	8.4	33.7 33.7	33.7	97.4 96.9	97.2	7.0 7.0	7.0	7.0	2.8 2.7	2.8	2.8	3.6 3.6	3.6	
C2	Sunny	Calm	09:32	Surface	1	22.6 22.6	22.6	8.3 8.4	8.4	33.3 33.3	33.3	98.9 99.6	99.3	7.1 7.1	7.1	7.1	1.5 1.4	1.5	1.7	4.9 5.0	5.0	5.6
				Middle	16.5	22.4 22.3	22.4	8.4 8.4	8.4	33.5 33.5	33.5	98.4 98.5	98.5	7.0 7.1	7.1	7.1	1.1 1.1	1.1	1.1	5.5 5.6	5.6	
				Bottom	32	22.2 22.2	22.2	8.4 8.4	8.4	33.6 33.6	33.6	97.0 97.1	97.1	7.0 7.0	7.0	7.0	2.6 2.6	2.6	2.6	6.4 6.2	6.3	
G1	Sunny	Calm	10:06	Surface	1	23.1 23.0	23.1	8.5 8.5	8.5	33.3 33.4	33.4	128.2 125.5	126.9	9.1 8.9	9.0	8.7	0.5 0.4	0.5	1.2	5.7 5.7	5.7	5.8
				Middle	4	22.5 22.6	22.6	8.5 8.5	8.5	33.5 33.5	33.5	116.6 118.5	117.6	8.3 8.4	8.4	8.4	1.5 1.5	1.5	1.5	5.1 5.1	5.1	
				Bottom	7	22.4 22.4	22.4	8.4 8.5	8.5	33.5 33.5	33.5	107.7 108.9	108.3	7.7 7.8	7.8	7.8	1.4 1.5	1.5	1.5	6.7 6.7	6.7	
G2	Sunny	Calm	09:55	Surface	1	23.0 23.0	23.0	8.5 8.5	8.5	33.4 33.4	33.4	135.4 131.7	133.6	9.6 9.3	9.5	9.1	0.4 0.5	0.5	0.9	5.4 5.5	5.5	6.1
				Middle	5	22.7 22.7	22.7	8.5 8.5	8.5	33.5 33.4	33.5	120.5 119.2	119.9	8.6 8.5	8.6	8.6	0.7 0.6	0.7	0.7	6.7 6.5	6.6	
				Bottom	9	22.3 22.3	22.3	8.4 8.4	8.4	33.5 33.5	33.5	105.3 104.2	104.8	7.5 7.5	7.5	7.5	1.4 1.5	1.5	1.5	6.2 6.3	6.3	
G3	Sunny	Calm	10:12	Surface	1	22.9 23.0	23.0	8.5 8.5	8.5	33.4 33.4	33.4	132.3 131.7	132.0	9.4 9.3	9.4	9.3	0.8 1.0	0.9	0.8	3.8 3.9	3.9	3.7
				Middle	3.5	22.7 22.8	22.8	8.5 8.5	8.5	33.5 33.4	33.5	126.1 130.1	128.1	9.0 9.2	9.1	9.1	0.7 0.8	0.8	0.8	2.6 2.5	2.6	
				Bottom	6	22.6 22.6	22.6	8.5 8.5	8.5	33.5 33.5	33.5	121.5 120.7	121.1	8.7 8.6	8.7	8.7	0.8 0.8	0.8	0.8	4.7 4.7	4.7	
G4	Sunny	Calm	10:25	Surface	1	23.1 23.0	23.1	8.5 8.5	8.5	33.4 33.4	33.4	136.5 130.7	133.6	9.6 9.2	9.4	8.7	0.6 0.7	0.7	1.5	5.2 5.0	5.1	4.4
				Middle	4	22.7 22.5	22.6	8.5 8.5	8.5	33.4 33.4	33.4	116.1 107.4	111.8	8.3 7.7	8.0	8.0	1.1 1.0	1.1	1.1	4.5 4.5	4.5	
				Bottom	7	22.4 22.5	22.5	8.4 8.4	8.4	33.5 33.5	33.5	99.9 102.8	101.4	7.1 7.3	7.2	7.2	2.7 2.7	2.7	2.7	3.7 3.5	3.6	
M1	Sunny	Calm	10:01	Surface	1	23.0 22.9	23.0	8.5 8.5	8.5	33.2 33.3	33.3	124.2 120.5	122.4	8.8 8.5	8.7	8.5	0.9 0.9	0.9	1.9	3.9 3.9	3.9	4.1
				Middle	3	22.6 22.8	22.7	8.5 8.5	8.5	33.5 33.4	33.5	115.2 117.1	116.2	8.2 8.3	8.3	8.3	1.7 1.8	1.8	1.8	4.2 4.3	4.3	
				Bottom	5	22.4 22.5	22.5	8.4 8.5	8.5	33.5 33.5	33.5	110.0 113.6	111.8	7.9 8.1	8.0	8.0	3.1 2.6	2.9	2.9	4.1 4.0	4.1	
M2	Sunny	Calm	09:50	Surface	1	22.7 22.6	22.7	8.5 8.4	8.5	33.4 33.4	33.4	117.5 113.4	115.5	8.4 8.1	8.3	8.3	0.7 0.7	0.7	1.0	4.5 4.3	4.4	4.6
				Middle	6	22.5 22.5	22.5	8.4 8.5	8.5	33.5 33.5	33.5	113.8 114.4	114.1	8.1 8.2	8.2	8.2	0.8 0.8	0.8	0.8	5.0 5.0	5.0	
				Bottom	11	22.3 22.3	22.3	8.4 8.4	8.4	33.5 33.5	33.5	102.8 103.3	103.1	7.4 7.4	7.4	7.4	1.5 1.4	1.5	1.5	4.3 4.3	4.3	
M3	Sunny	Calm	10:18	Surface	1	22.9 23.0	23.0	8.5 8.5	8.5	33.3 33.3	33.3	130.9 131.3	131.1	9.3 9.3	9.3	9.5	0.8 1.0	0.9	0.9	3.0 2.9	3.0	4.5
				Middle	3.5	22.9 22.8	22.9	8.5 8.5	8.5	33.5 33.5	33.5	136.6 135.7	136.2	9.7 9.6	9.7	9.7	0.7 0.8	0.8	0.8	4.8 4.8	4.8	
				Bottom	6	22.8 22.7	22.8	8.5 8.5	8.5	33.5 33.5	33.5	130.2 126.9	128.6	9.3 9.0	9.2	9.2	0.8 0.9	0.9	0.9	5.6 5.6	5.6	
M4	Sunny	Calm	09:41	Surface	1	22.5 22.5	22.5	8.4 8.4	8.4	33.4 33.4	33.4	99.7 100.1	99.9	7.1 7.2	7.2	7.2	1.6 1.6	1.6	1.7	4.1 4.1	4.1	5.0
				Middle	5	22.3 22.4	22.4	8.4 8.4	8.4	33.6 33.5	33.6	99.3 99.6	99.5	7.1 7.1	7.1	7.1	1.6 1.6	1.6	1.6	4.4 4.5	4.5	
				Bottom	9	22.2 22.2	22.2	8.4 8.4	8.4	33.6 33.6	33.6	99.0 99.1	99.1	7.1 7.1	7.1	7.1	1.8 1.8	1.8	1.8	6.2 6.4	6.3	
M5	Sunny	Calm	10:37	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.4 33.4	33.4	105.9 105.3	105.6	7.6 7.5	7.6	7.5	0.8 0.9	0.9	1.3	5.1 5.1	5.1	5.6
				Middle	5	22.4 22.4	22.4	8.4 8.4	8.4	33.4 33.5	33.5	102.4 101.1	101.8	7.3 7.2	7.3	7.3	1.2 1.4	1.3	1.3	4.9 4.8	4.9	
				Bottom	9	22.3 22.3	22.3	8.4 8.4	8.4	33.6 33.6	33.6	99.0 98.6	98.8	7.1 7.1	7.1	7.1	1.7 1.9	1.8	1.8	6.7 6.8	6.8	
M6	Sunny	Calm	10:30	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	0.9	-	-	4.5
				Middle	2.1	22.5 22.5	22.5	8.4 8.4	8.4	33.4 33.4	33.4	102.9 103.6	103.3	7.3 7.4	7.4	7.4	0.9 0.8	0.9	0.9	4.5 4.5	4.5	
				Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 12 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 4.6 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 4.9 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.2 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.2 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 8.0 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 8.7 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 12 April 2018**

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity (NTU)			Suspended Solids (mg/L)						
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
C1	Sunny	Calm	15:21	Surface	1	22.7 22.9	22.8	8.4 8.4	8.4	33.3 33.3	33.3	103.6 104.5	104.1	7.4 7.4	7.4	7.4	7.4	0.9 0.9	0.9	7.4	1.1 0.9	1.1	5.5 5.4	5.5	5.9	
				Middle	9.5	22.5 22.5	22.5	8.4 8.4	8.4	33.5 33.4	33.5	101.2 102.4	101.8	7.2 7.3	7.3	7.3	7.3	7.3	1.0 1.0	1.0	7.4	1.1 1.0	1.1	5.5 5.4		5.5
				Bottom	18	22.2 22.2	22.2	8.4 8.4	8.4	33.8 33.8	33.8	95.8 96.2	96.0	6.9 6.9	6.9	6.9	6.9	6.9	6.9	3.9 3.6	3.8	7.4	1.1 1.1	1.1		6.6 6.8
C2	Sunny	Calm	14:10	Surface	1	22.9 22.9	22.9	8.4 8.4	8.4	33.2 33.2	33.2	97.7 98.3	98.0	6.9 7.0	7.0	7.0	7.0	1.1 1.1	1.1	7.0	1.1 1.1	1.1	4.5 4.4	4.5	4.4	
				Middle	17	22.4 22.4	22.4	8.4 8.4	8.4	33.5 33.5	33.5	95.8 95.9	95.9	6.9 6.9	6.9	6.9	6.9	6.9	1.8 1.7	1.8	7.0	1.1 1.1	1.1	3.9 3.8		3.9
				Bottom	33	22.2 22.2	22.2	8.4 8.4	8.4	33.6 33.6	33.6	95.5 95.7	95.6	6.8 6.9	6.9	6.9	6.9	6.9	1.9 2.0	2.0	7.0	1.1 1.1	1.1	4.7 4.7		4.7
G1	Sunny	Calm	14:42	Surface	1	23.7 23.8	23.8	8.6 8.6	8.6	33.4 33.4	33.4	149.8 148.5	149.2	10.5 10.4	10.5	10.4	10.4	0.5 0.5	0.5	10.4	0.5 0.5	0.5	5.1 4.8	5.0	4.7	
				Middle	4	23.4 23.5	23.5	8.6 8.6	8.6	33.4 33.4	33.4	146.8 147.4	147.1	10.3 10.3	10.3	10.3	10.3	0.5 0.5	0.5	10.4	0.5 0.5	0.5	6.1 5.9	6.0		
				Bottom	7	22.4 22.4	22.4	8.4 8.5	8.5	33.5 33.5	33.5	108.7 107.9	108.3	7.8 7.7	7.8	7.8	7.8	7.8	1.6 1.9	1.8	10.4	0.5 0.5	0.5	3.0 3.0		3.0
G2	Sunny	Calm	14:31	Surface	1	23.7 23.8	23.8	8.6 8.6	8.6	33.4 33.4	33.4	149.1 142.3	145.7	10.4 9.9	10.2	10.2	10.2	0.6 0.6	0.6	9.9	0.6 0.6	0.6	3.4 3.3	3.4	4.1	
				Middle	5	22.9 22.8	22.9	8.6 8.6	8.6	33.4 33.4	33.4	135.0 133.1	134.1	9.6 9.4	9.5	9.5	9.5	1.1 1.2	1.2	9.9	0.6 0.6	0.6	4.7 4.6	4.7		
				Bottom	9	22.3 22.3	22.3	8.4 8.5	8.5	33.5 33.5	33.5	107.0 107.5	107.3	7.7 7.7	7.7	7.7	7.7	1.7 1.5	1.6	9.9	0.6 0.6	0.6	4.0 4.1	4.1		
G3	Sunny	Calm	14:48	Surface	1	23.7 23.7	23.7	8.6 8.6	8.6	33.2 33.2	33.2	142.6 143.3	143.0	10.0 10.0	10.0	10.0	10.0	0.7 0.8	0.8	9.9	0.7 0.8	0.8	5.4 5.2	5.3	5.4	
				Middle	3.5	23.3 23.2	23.3	8.6 8.6	8.6	33.3 33.3	33.3	138.3 140.7	139.5	9.7 9.9	9.8	9.8	9.8	0.8 0.9	0.9	9.9	0.7 0.8	0.8	5.6 5.4	5.5		
				Bottom	6	22.5 22.6	22.6	8.5 8.5	8.5	33.5 33.5	33.5	117.2 116.9	117.1	8.4 8.3	8.4	8.4	8.4	0.8 0.7	0.8	9.9	0.7 0.7	0.8	5.5 5.5	5.5		
G4	Sunny	Calm	15:00	Surface	1	23.4 23.5	23.5	8.5 8.5	8.5	33.4 33.4	33.4	133.0 131.6	132.3	9.3 9.2	9.3	9.3	9.3	1.2 1.1	1.2	9.3	1.2 1.1	1.2	4.7 4.6	4.7	6.4	
				Middle	4	23.4 23.4	23.4	8.5 8.5	8.5	33.4 33.4	33.4	131.9 132.8	132.4	9.3 9.3	9.3	9.3	9.3	1.1 1.1	1.1	9.3	1.2 1.1	1.1	10.6 10.6	10.6		
				Bottom	7	22.3 22.4	22.4	8.4 8.4	8.4	33.5 33.5	33.5	97.8 100.0	98.9	7.0 7.2	7.1	7.1	7.1	3.9 3.8	3.9	9.3	1.2 1.1	1.1	3.8 3.8	3.8		
M1	Sunny	Calm	14:37	Surface	1	23.8 23.7	23.8	8.6 8.6	8.6	33.4 33.4	33.4	150.1 148.4	149.3	10.5 10.4	10.5	10.5	10.3	0.4 0.4	0.4	10.3	0.4 0.4	0.4	4.2 4.1	4.2	4.5	
				Middle	3	23.7 23.4	23.6	8.6 8.6	8.6	33.4 33.4	33.4	149.3 138.8	144.1	10.4 9.8	10.1	10.1	10.1	0.6 0.6	0.6	10.3	0.4 0.4	0.4	3.0 3.1	3.1		
				Bottom	5	23.1 22.9	23.0	8.5 8.5	8.5	33.4 33.4	33.4	130.7 134.2	132.5	9.2 9.5	9.4	9.4	9.4	1.0 0.8	0.9	10.3	0.4 0.4	0.4	6.1 6.0	6.1		
M2	Sunny	Calm	14:24	Surface	1	23.6 23.6	23.6	8.6 8.6	8.6	33.4 33.4	33.4	151.3 143.2	147.3	10.6 10.0	10.3	10.3	9.9	1.0 1.0	1.0	9.9	1.0 1.0	1.0	5.3 5.3	5.3	4.6	
				Middle	6	23.1 22.7	22.9	8.6 8.5	8.6	33.4 33.5	33.5	138.7 126.2	132.5	9.8 9.0	9.4	9.4	9.4	1.0 1.1	1.1	9.9	1.0 1.0	1.0	5.7 5.7	5.7		
				Bottom	11	22.2 22.2	22.2	8.4 8.4	8.4	33.6 33.6	33.6	97.9 97.3	97.6	7.0 7.0	7.0	7.0	7.0	3.4 3.4	3.4	9.9	1.0 1.0	1.0	2.7 2.7	2.7		
M3	Sunny	Calm	14:53	Surface	1	24.0 24.0	24.0	8.6 8.6	8.6	33.3 33.3	33.3	153.0 151.4	152.2	10.7 10.5	10.6	10.6	10.2	0.5 0.5	0.5	10.2	0.5 0.5	0.5	4.8 4.8	4.8	6.4	
				Middle	3.5	23.2 23.4	23.3	8.6 8.6	8.6	33.3 33.3	33.3	139.1 139.9	139.5	9.8 9.8	9.8	9.8	9.8	1.2 1.1	1.2	10.2	0.5 0.5	0.5	7.8 7.7	7.8		
				Bottom	6	22.6 22.6	22.6	8.5 8.5	8.5	33.5 33.5	33.5	119.0 115.9	117.5	8.5 8.3	8.4	8.4	8.4	1.3 1.1	1.2	10.2	0.5 0.5	0.5	6.5 6.4	6.5		
M4	Sunny	Calm	14:18	Surface	1	23.6 23.6	23.6	8.5 8.5	8.5	33.4 33.4	33.4	135.5 134.3	134.9	9.5 9.4	9.5	9.5	9.5	0.5 0.5	0.5	9.5	0.5 0.5	0.5	4.9 4.8	4.9	5.4	
				Middle	5	23.4 23.3	23.4	8.5 8.5	8.5	33.4 33.4	33.4	133.5 134.8	134.2	9.4 9.5	9.5	9.5	9.5	0.6 0.6	0.6	9.5	0.5 0.5	0.5	5.0 5.0	5.0		
				Bottom	9	22.7 22.9	22.8	8.5 8.5	8.5	33.5 33.4	33.5	122.3 125.0	123.7	8.7 8.9	8.8	8.8	8.8	1.0 0.9	1.0	9.5	0.5 0.5	0.5	6.4 6.4	6.4		
M5	Sunny	Calm	15:13	Surface	1	22.8 22.9	22.9	8.4 8.4	8.4	33.4 33.3	33.4	106.3 107.0	106.7	7.5 7.6	7.6	7.6	7.6	0.9 0.9	0.9	7.6	0.9 0.9	0.9	6.1 6.0	6.1	5.6	
				Middle	5	22.7 22.5	22.6	8.4 8.4	8.4	33.4 33.4	33.4	105.2 103.7	104.5	7.5 7.4	7.5	7.5	7.5	1.2 1.3	1.3	7.6	0.9 0.9	0.9	4.1 4.2	4.2		
				Bottom	9	22.5 22.5	22.5	8.4 8.4	8.4	33.4 33.5	33.5	101.6 101.9	101.8	7.3 7.3	7.3	7.3	7.3	1.2 1.3	1.3	7.6	0.9 0.9	0.9	6.2 6.5	6.4		
M6	Sunny	Calm	15:06	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	7.0	
				Middle	2.1	23.5 23.4	23.5	8.5 8.5	8.5	33.3 33.4	33.4	133.6 132.3	133.0	9.4 9.3	9.4	9.4	9.4	0.6 0.6	0.6	9.4	0.6 0.6	0.6	7.0 6.9	7.0		
				Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 14 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.2 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.5 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.0 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.5 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.0 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.5 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.6 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 8.2 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 14 April 2018**

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition*	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Cloudy	Calm	12:00	Surface	1	22.9 22.9	22.9	8.2 8.2	8.2	33.5 33.5	33.5	101.0 100.9	101.0	7.2 7.1	7.2	7.2	1.3 1.3	1.3	1.4	4.5 4.5	4.5	5.4
				Middle	9	22.9 22.9	22.9	8.2 8.2	8.2	33.6 33.6	33.6	101.1 100.8	101.0	7.2 7.1	7.2		1.2 1.2	1.2		6.0 6.0	6.0	
				Bottom	17	22.6 22.6	22.6	8.3 8.3	8.3	34.0 34.0	34.0	98.8 98.7	98.8	7.0 7.0	7.0		1.7 1.6	1.7		5.8 5.7	5.8	
C2	Cloudy	Calm	10:56	Surface	1	23.0 23.0	23.0	8.1 8.2	8.2	33.3 33.4	33.4	98.5 98.0	98.3	7.0 6.9	7.0	7.0	1.3 1.5	1.4	2.1	5.0 4.9	5.0	5.3
				Middle	16.5	22.7 22.7	22.7	8.2 8.2	8.2	33.7 33.7	33.7	97.3 97.5	97.4	6.9 6.9	6.9		2.2 1.9	2.1		4.5 4.4	4.5	
				Bottom	32	22.6 22.6	22.6	8.2 8.2	8.2	33.8 33.9	33.9	97.1 96.8	97.0	6.9 6.9	6.9		2.7 2.6	2.7		6.2 6.4	6.3	
G1	Cloudy	Calm	11:26	Surface	1	23.7 23.7	23.7	8.3 8.3	8.3	33.3 33.3	33.3	123.3 122.5	122.9	8.6 8.6	8.6	8.3	0.6 0.7	0.7	1.0	5.2 5.4	5.3	5.5
				Middle	4	22.8 22.8	22.8	8.3 8.3	8.3	33.6 33.6	33.6	113.7 111.0	112.4	8.1 7.9	8.0		1.0 1.0	1.0		5.2 5.5	5.4	
				Bottom	7	22.8 22.7	22.8	8.2 8.2	8.2	33.7 33.8	33.8	104.3 102.1	103.2	7.4 7.3	7.4		1.1 1.2	1.2		5.7 5.9	5.8	
G2	Cloudy	Calm	11:15	Surface	1	23.1 23.3	23.2	8.3 8.3	8.3	33.5 33.5	33.5	118.9 121.0	120.0	8.4 8.5	8.5	8.2	0.8 0.7	0.8	1.0	4.3 4.4	4.4	4.4
				Middle	5	22.8 22.9	22.9	8.2 8.3	8.3	33.6 33.6	33.6	107.1 111.0	109.1	7.6 7.9	7.8		0.8 0.8	0.9		3.0 3.9	3.5	
				Bottom	9	22.7 22.7	22.7	8.2 8.2	8.2	33.8 33.8	33.8	100.2 99.9	100.1	7.1 7.1	7.1		1.3 1.2	1.3		5.2 5.4	5.3	
G3	Cloudy	Calm	11:32	Surface	1	23.4 23.6	23.5	8.3 8.3	8.3	33.4 33.3	33.4	129.1 131.6	130.4	9.1 9.2	9.2	8.9	0.7 0.7	0.7	0.9	3.2 3.3	3.3	3.8
				Middle	4	23.0 23.0	23.0	8.3 8.3	8.3	33.5 33.5	33.5	121.3 122.1	121.7	8.6 8.6	8.6		0.8 0.8	0.8		4.0 4.1	4.1	
				Bottom	7	22.7 22.7	22.7	8.2 8.3	8.3	33.6 33.6	33.6	108.1 109.6	108.9	7.7 7.8	7.8		1.3 1.2	1.3		4.0 3.9	4.0	
G4	Cloudy	Calm	11:41	Surface	1	23.5 23.6	23.7	8.3 8.3	8.3	33.3 33.1	33.2	121.3 119.1	120.2	8.5 8.3	8.4	8.1	0.5 0.6	0.6	1.5	3.4 3.6	3.5	5.2
				Middle	4	22.9 22.9	22.9	8.3 8.2	8.3	33.5 33.5	33.5	110.3 105.7	108.0	7.8 7.5	7.7		0.9 1.0	1.0		5.6 5.7	5.7	
				Bottom	7	22.6 22.6	22.6	8.2 8.2	8.2	33.9 33.9	33.9	98.7 97.8	98.3	7.0 7.0	7.0		3.0 2.7	2.9		6.3 6.2	6.3	
M1	Cloudy	Calm	11:22	Surface	1	23.7 23.7	23.7	8.3 8.3	8.3	33.4 33.3	33.4	124.4 123.2	123.8	8.7 8.6	8.7	8.4	0.6 0.7	0.7	1.1	3.3 3.4	3.4	4.0
				Middle	3	22.9 23.0	23.0	8.3 8.3	8.3	33.6 33.6	33.6	112.0 114.0	113.0	7.9 8.1	8.0		1.2 1.2	1.2		4.0 4.0	4.0	
				Bottom	5	22.9 22.9	22.9	8.3 8.3	8.3	33.6 33.6	33.6	109.5 110.5	110.0	7.8 7.8	7.8		1.3 1.4	1.4		4.5 4.9	4.7	
M2	Cloudy	Calm	11:10	Surface	1	23.1 22.9	23.0	8.2 8.2	8.2	33.6 33.6	33.6	105.8 105.7	105.8	7.5 7.5	7.5	7.5	0.9 0.9	0.9	1.3	5.2 5.2	5.2	4.9
				Middle	6	22.8 22.8	22.8	8.2 8.2	8.2	33.6 33.6	33.6	102.9 103.6	103.3	7.3 7.4	7.4		1.0 1.1	1.1		3.7 3.7	3.7	
				Bottom	11	22.6 22.6	22.6	8.2 8.2	8.2	33.9 33.9	33.9	98.4 97.6	98.0	7.0 6.9	7.0		1.9 2.1	2.0		5.7 5.7	5.7	
M3	Cloudy	Calm	11:36	Surface	1	23.3 23.7	23.5	8.3 8.3	8.3	33.4 33.2	33.3	127.7 130.1	128.9	9.0 9.1	9.1	8.7	0.8 0.8	0.8	1.2	5.6 5.6	5.6	5.2
				Middle	4	23.0 22.9	23.0	8.3 8.3	8.3	33.5 33.5	33.5	116.0 114.7	115.4	8.2 8.1	8.2		1.0 1.1	1.1		5.7 5.6	5.7	
				Bottom	7	22.6 22.6	22.6	8.2 8.2	8.2	33.7 33.6	33.7	99.4 100.0	99.7	7.1 7.1	7.1		1.7 1.8	1.8		4.3 4.3	4.3	
M4	Cloudy	Calm	11:03	Surface	1	23.0 22.9	23.0	8.2 8.2	8.2	33.6 33.7	33.7	101.6 103.4	102.5	7.2 7.3	7.3	7.2	1.5 1.5	1.5	2.0	5.2 5.1	5.2	5.9
				Middle	5	22.6 22.6	22.6	8.2 8.2	8.2	33.8 33.8	33.8	98.5 98.4	98.5	7.0 7.0	7.0		2.2 2.1	2.2		5.7 5.7	5.7	
				Bottom	9	22.6 22.6	22.6	8.2 8.2	8.2	33.8 33.8	33.8	98.1 98.1	98.1	7.0 7.0	7.0		2.4 2.4	2.4		6.8 6.6	6.7	
M5	Cloudy	Calm	11:54	Surface	1	23.4 23.4	23.4	8.2 8.2	8.2	33.5 33.5	33.5	110.2 107.6	108.9	7.7 7.6	7.7	7.6	0.9 0.9	0.9	1.4	5.3 5.4	5.4	5.2
				Middle	5.5	22.8 22.8	22.8	8.2 8.2	8.2	33.6 33.6	33.6	104.8 103.9	104.4	7.4 7.4	7.4		1.2 1.3	1.3		5.2 5.1	5.2	
				Bottom	10	22.7 22.7	22.7	8.2 8.2	8.2	33.7 33.7	33.7	98.7 98.4	98.6	7.0 7.0	7.0		2.0 2.1	2.1		5.1 5.1	5.1	
M6	Cloudy	Calm	11:48	Surface	-	-	-	-	-	-	-	-	-	-	-	7.2	-	-	1.1	-	-	4.8
				Middle	2	22.9 22.9	22.9	8.2 8.2	8.2	33.5 33.5	33.5	102.1 102.0	102.1	7.2 7.2	7.2		1.1 1.1	1.1		4.9 4.7	4.8	
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-	

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 14 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 5.5 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 6.0 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.9 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.9 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.2 mg/L</u>
<u>Station M6</u>			
Intake Level		<u>8.3 mg/L</u>	<u>8.6 mg/L</u>

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 14 April 2018

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Cloudy	Calm	17:05	Surface	1	23.2 23.1	23.2	8.2 8.2	8.2	33.3 33.4	33.4	98.5 97.7	98.1	7.0 6.9	7.0	7.1	1.2 1.3	1.3	2.6	5.2 5.4	5.3	4.6
				Middle	10	22.7 22.7	22.7	8.2 8.2	8.2	33.9 33.8	33.9	99.3 97.8	98.6	7.1 7.0	7.1		2.0 1.9	2.0		3.0 2.9	3.0	
				Bottom	19	22.5 22.5	22.5	8.2 8.2	8.2	34.0 34.0	34.0	96.2 96.2	96.2	6.8 6.8	6.8		4.6 4.6	4.6		5.4 5.6	5.5	
C2	Cloudy	Calm	16:07	Surface	1	23.4 23.4	23.4	8.1 8.1	8.1	33.0 33.1	33.1	93.6 96.4	95.0	6.6 6.8	6.7	6.7	1.5 1.6	1.6	1.9	3.7 3.8	3.8	5.0
				Middle	17	23.0 23.4	23.2	8.1 8.1	8.1	33.4 33.1	33.3	92.5 96.5	94.5	6.6 6.8	6.7		2.1 1.9	2.0		6.3 6.5	6.4	
				Bottom	33	23.0 23.3	23.2	8.2 8.2	8.2	33.4 33.2	33.3	92.2 96.1	94.2	6.5 6.8	6.7		2.1 1.9	2.0		5.0 4.8	4.9	
G1	Cloudy	Calm	16:34	Surface	1	23.7 23.8	23.8	8.3 8.3	8.3	33.4 33.4	33.4	131.3 135.2	133.3	9.2 9.4	9.3	9.1	0.8 0.7	0.8	1.0	5.6 5.8	5.7	4.3
				Middle	4	23.5 23.5	23.5	8.3 8.3	8.3	33.4 33.4	33.4	126.1 127.1	126.6	8.9 8.9	8.9		0.9 0.8	0.9		4.1 4.2	4.2	
				Bottom	7	23.0 23.0	23.0	8.3 8.3	8.3	33.5 33.5	33.5	115.3 119.6	117.5	8.2 8.5	8.4		1.2 1.2	1.2		3.0 3.0	3.0	
G2	Cloudy	Calm	16:25	Surface	1	23.5 23.6	23.6	8.3 8.3	8.3	33.4 33.4	33.4	129.3 130.9	130.1	9.1 9.2	9.2	9.1	0.9 0.9	0.9	1.3	5.2 5.1	5.2	5.4
				Middle	5	23.3 23.3	23.3	8.3 8.3	8.3	33.5 33.5	33.5	125.5 125.8	125.7	8.8 8.9	8.9		1.4 1.3	1.4		4.6 4.6	4.6	
				Bottom	9	22.7 22.7	22.7	8.2 8.3	8.3	33.7 33.6	33.7	103.8 110.3	107.1	7.4 7.8	7.6		1.6 1.6	1.6		6.4 6.4	6.4	
G3	Cloudy	Calm	16:39	Surface	1	24.2 24.2	24.2	8.4 8.4	8.4	33.1 33.2	33.2	139.4 143.4	141.4	9.7 10.0	9.9	9.6	0.8 0.8	0.8	0.9	3.6 3.4	3.5	4.1
				Middle	4	23.5 23.5	23.5	8.3 8.3	8.3	33.3 33.3	33.3	131.6 133.2	132.4	9.2 9.5	9.3		0.9 0.8	0.9		3.5 3.6	3.6	
				Bottom	7	23.0 23.0	23.0	8.3 8.3	8.3	33.5 33.5	33.5	119.8 118.2	119.0	8.5 8.4	8.5		1.1 1.1	1.1		5.1 5.0	5.1	
G4	Cloudy	Calm	16:49	Surface	1	23.5 23.5	23.5	8.3 8.3	8.3	33.5 33.5	33.5	126.9 127.2	127.1	8.9 8.9	8.9	8.9	0.7 0.6	0.8	1.1	4.3 4.3	4.3	4.1
				Middle	4	23.4 23.4	23.4	8.3 8.3	8.3	33.5 33.5	33.5	126.7 124.2	125.5	8.9 8.7	8.8		0.8 0.9	0.9		2.9 2.8	2.9	
				Bottom	7	23.1 23.0	23.1	8.3 8.2	8.3	33.6 33.6	33.6	111.7 111.3	111.5	7.9 7.9	7.9		1.7 1.6	1.7		5.0 4.9	5.0	
M1	Cloudy	Calm	16:30	Surface	1	23.9 23.9	23.9	8.3 8.3	8.3	33.4 33.4	33.4	135.5 136.9	136.2	9.5 9.5	9.5	9.5	0.9 1.0	1.0	1.1	5.7 5.7	5.7	4.5
				Middle	3	23.6 23.7	23.7	8.3 8.3	8.3	33.4 33.4	33.4	133.8 134.4	134.1	9.4 9.4	9.4		0.9 0.8	0.9		3.6 3.4	3.5	
				Bottom	5	23.4 23.5	23.5	8.3 8.3	8.3	33.4 33.4	33.4	128.6 127.5	128.1	9.0 9.0	9.0		1.3 1.4	1.4		4.2 4.2	4.2	
M2	Cloudy	Calm	16:20	Surface	1	23.5 23.5	23.5	8.3 8.3	8.3	33.5 33.5	33.5	127.0 128.9	128.0	8.9 9.0	9.0	8.8	0.8 0.8	0.8	1.2	5.0 5.0	5.0	5.2
				Middle	6	23.2 23.3	23.3	8.3 8.3	8.3	33.5 33.5	33.5	120.3 123.9	122.1	8.5 8.7	8.6		1.0 1.0	1.0		5.7 5.7	5.7	
				Bottom	11	22.7 22.7	22.7	8.3 8.3	8.3	33.8 33.8	33.8	105.2 103.7	104.5	7.5 7.4	7.5		1.6 1.8	1.7		4.9 4.7	4.8	
M3	Cloudy	Calm	16:43	Surface	1	24.1 24.1	24.1	8.3 8.3	8.3	33.1 33.2	33.2	140.8 142.1	141.5	9.8 9.9	9.9	9.6	1.1 0.9	1.0	1.1	5.4 5.4	5.4	5.7
				Middle	4	23.5 23.5	23.5	8.3 8.3	8.3	33.3 33.3	33.3	130.7 130.5	130.6	9.2 9.2	9.2		1.1 1.2	1.2		7.4 7.7	7.6	
				Bottom	7	23.0 23.0	23.0	8.3 8.3	8.3	33.5 33.5	33.5	120.7 120.5	120.6	8.5 8.5	8.5		1.0 1.0	1.0		4.1 4.1	4.1	
M4	Cloudy	Calm	16:14	Surface	1	23.8 23.9	23.9	8.3 8.3	8.3	33.5 33.5	33.5	136.6 136.4	136.5	9.5 9.5	9.5	9.1	0.7 0.8	0.8	0.9	5.6 5.9	5.8	5.5
				Middle	5	23.1 23.1	23.1	8.3 8.3	8.3	33.5 33.5	33.5	120.4 122.1	121.3	8.5 8.6	8.6		0.8 0.8	0.8		4.8 4.7	4.8	
				Bottom	9	22.9 22.9	22.9	8.2 8.2	8.2	33.7 33.6	33.7	106.1 108.2	107.2	7.5 7.7	7.6		1.1 1.0	1.1		5.9 5.9	5.9	
M5	Cloudy	Calm	16:59	Surface	1	23.2 23.2	23.2	8.2 8.2	8.2	33.3 33.3	33.3	103.1 101.0	102.1	7.3 7.1	7.2	7.2	1.3 1.2	1.3	1.6	4.8 5.1	5.0	4.9
				Middle	5.5	23.1 23.0	23.1	8.2 8.2	8.2	33.4 33.4	33.4	100.2 99.5	99.9	7.1 7.0	7.1		1.2 1.2	1.2		4.6 4.7	4.7	
				Bottom	10	22.9 22.9	22.9	8.2 8.2	8.2	33.5 33.5	33.5	98.9 98.5	98.7	7.0 7.0	7.0		2.5 2.2	2.4		5.0 5.0	5.0	
M6	Cloudy	Calm	16:54	Surface	-	-	-	-	-	-	-	-	-	-	-	8.7	-	-	1.0	-	-	6.8
				Middle	2	23.4 23.4	23.4	8.3 8.3	8.3	33.5 33.5	33.5	123.5 124.0	123.8	8.7 8.7	8.7		1.0 1.0	1.0		6.8 6.7	6.8	
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-	

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 16 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.1 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.4 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.2 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.8 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.2 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.8 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.8 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 8.5 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 16 April 2018**

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
C1	Rainy	Calm	13:57	Surface	1	22.8 22.8	22.8	8.4 8.4	8.4	33.5 33.5	33.5	88.8 88.8	88.9	6.3 6.3	6.3	6.3	6.3	1.8 3.0	2.9	3.0	3.9 3.9	3.9	5.7
				Middle	10	22.8 22.8	22.8	8.4 8.4	8.4	33.5 33.5	33.5	88.8 88.8	88.8	6.3 6.3	6.3	3.0		3.0	6.9 6.8		6.9		
				Bottom	19	22.7 22.7	22.7	8.4 8.4	8.4	33.6 33.6	33.6	89.2 90.2	89.7	6.3 6.4	6.4	3.0 3.0		3.0	6.3 6.4		6.4		
C2	Rainy	Calm	12:33	Surface	1	22.8 22.8	22.8	8.4 8.3	8.4	33.4 33.3	33.4	88.7 88.4	88.6	6.3 6.3	6.3	6.3	1.8 1.9	1.9	2.2	5.1 5.2	5.2	5.4	
				Middle	17	22.8 22.8	22.8	8.3 8.3	8.3	33.4 33.4	33.4	88.4 88.2	88.3	6.3 6.3	6.3		2.1 2.0	2.1		4.4 4.3	4.4		
				Bottom	33	22.8 22.8	22.8	8.3 8.3	8.3	33.4 33.4	33.4	88.4 88.5	88.5	6.3 6.3	6.3		2.6 2.6	2.6		6.5 6.4	6.5		
G1	Rainy	Calm	13:08	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.6	33.6	91.9 92.1	92.0	6.5 6.6	6.6	6.6	0.8 0.9	0.9	0.9	3.5 3.4	3.5	5.6	
				Middle	3	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.7	33.7	92.2 92.5	92.4	6.6 6.6	6.6		0.9 0.8	0.9		8.2 8.1	8.2		
				Bottom	5	22.7 22.7	22.7	8.4 8.4	8.4	33.7 33.7	33.7	93.2 93.5	93.4	6.6 6.7	6.7		1.0 0.9	1.0		5.0 5.1	5.1		
G2	Rainy	Calm	12:57	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	93.5 92.8	93.2	6.7 6.6	6.7	6.7	1.4 1.3	1.4	1.4	4.8 4.9	4.9	6.0	
				Middle	4.5	22.7 22.6	22.7	8.4 8.4	8.4	33.7 33.7	33.7	92.3 92.6	92.5	6.6 6.6	6.6		1.3 1.3	1.3		6.5 6.4	6.5		
				Bottom	8	22.7 22.7	22.7	8.4 8.4	8.4	33.8 33.8	33.8	91.3 91.1	91.2	6.5 6.5	6.5		1.5 1.5	1.5		6.5 6.7	6.6		
G3	Rainy	Calm	13:15	Surface	1	22.7 22.7	22.7	8.4 8.4	8.4	33.6 33.6	33.6	90.5 91.5	91.0	6.4 6.5	6.5	6.5	1.8 1.6	1.7	1.4	5.5 5.4	5.5	5.3	
				Middle	3.5	22.7 22.7	22.7	8.4 8.4	8.4	33.7 33.7	33.7	91.9 92.1	92.0	6.5 6.5	6.5		1.5 1.5	1.5		5.9 5.4	5.7		
				Bottom	6	22.7 22.7	22.7	8.4 8.4	8.4	33.7 33.7	33.7	91.1 92.1	91.6	6.5 6.5	6.5		1.2 1.0	1.1		4.8 4.7	4.8		
G4	Rainy	Calm	13:28	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.6	33.6	92.9 92.8	92.9	6.6 6.6	6.6	6.6	1.1 1.0	1.1	1.2	5.2 5.2	5.2	5.4	
				Middle	4	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.6	33.6	92.5 92.7	92.6	6.6 6.6	6.6		1.2 1.1	1.2		5.5 5.4	5.5		
				Bottom	7	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.7	33.7	92.2 92.4	92.3	6.6 6.6	6.6		1.3 1.4	1.4		5.3 5.6	5.5		
M1	Rainy	Calm	13:03	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.6	33.6	93.1 92.3	92.7	6.6 6.6	6.6	6.7	1.3 1.4	1.4	1.3	5.7 5.9	5.8	5.2	
				Middle	3	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	93.5 93.3	93.4	6.7 6.6	6.7		1.2 1.1	1.2		4.4 4.4	4.4		
				Bottom	5	22.7 22.7	22.7	8.4 8.4	8.4	33.7 33.7	33.7	93.0 93.1	93.1	6.6 6.6	6.6		1.2 1.3	1.3		5.3 5.3	5.3		
M2	Rainy	Calm	12:50	Surface	1	22.6 22.7	22.7	8.4 8.4	8.4	33.7 33.7	33.7	94.0 92.9	93.5	6.7 6.6	6.7	6.6	1.0 1.0	1.0	1.3	4.9 4.7	4.8	5.3	
				Middle	5.5	22.7 22.7	22.7	8.4 8.4	8.4	33.7 33.7	33.7	92.0 91.6	91.8	6.5 6.5	6.5		1.3 1.1	1.2		4.9 4.6	4.8		
				Bottom	10	22.7 22.7	22.7	8.4 8.4	8.4	33.8 33.8	33.8	90.2 90.7	90.5	6.4 6.4	6.4		1.7 1.7	1.7		6.1 6.2	6.2		
M3	Rainy	Calm	13:19	Surface	1	22.7 22.7	22.7	8.4 8.4	8.4	33.1 33.3	33.2	88.1 89.1	88.6	6.3 6.3	6.3	6.4	1.1 1.1	1.1	1.2	4.0 4.3	4.2	4.0	
				Middle	3	22.7 22.7	22.7	8.4 8.4	8.4	33.3 33.7	33.5	88.2 92.0	90.1	6.3 6.5	6.4		1.0 0.9	1.0		3.5 3.6	3.6		
				Bottom	5	22.7 22.8	22.8	8.4 8.4	8.4	33.8 33.8	33.8	90.7 88.1	89.4	6.4 6.3	6.4		1.6 1.6	1.6		4.0 4.2	4.1		
M4	Rainy	Calm	12:40	Surface	1	22.7 22.7	22.7	8.4 8.4	8.4	33.6 33.6	33.6	91.5 91.1	91.3	6.5 6.5	6.5	6.5	1.6 1.8	1.7	2.1	5.5 5.6	5.6	6.2	
				Middle	5.5	22.7 22.7	22.7	8.4 8.4	8.4	33.7 33.6	33.7	91.3 90.7	91.0	6.5 6.4	6.5		2.2 2.1	2.2		6.5 6.4	6.5		
				Bottom	10	22.7 22.7	22.7	8.4 8.4	8.4	33.8 33.7	33.8	91.2 90.6	90.9	6.5 6.4	6.5		2.5 2.5	2.5		6.5 6.6	6.6		
M5	Rainy	Calm	13:46	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.6	33.6	94.2 93.9	94.1	6.7 6.7	6.7	6.7	1.1 1.0	1.1	1.0	4.8 4.8	4.8	5.3	
				Middle	5	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	94.2 93.9	94.1	6.7 6.7	6.7		0.9 1.0	1.0		5.5 5.7	5.6		
				Bottom	9	22.7 22.6	22.7	8.4 8.4	8.4	33.8 33.7	33.8	93.5 94.0	93.8	6.6 6.7	6.7		0.9 0.9	0.9		5.5 5.5	5.5		
M6	Rainy	Calm	13:37	Surface	-	-	-	-	-	-	-	-	-	-	-	6.4	-	-	2.1	-	-	6.4	
				Middle	2	22.7 22.7	22.7	8.4 8.4	8.4	33.8 33.8	33.8	89.9 89.8	89.9	6.4 6.4	6.4		2.1 2.1	2.1		6.4 6.4	6.4		
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 16 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 2.6 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 2.9 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.1 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.1 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.6 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 8.2 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 16 April 2018

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)	Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity (NTU)			Suspended Solids (mg/L)				
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
C1	Rainy	Calm	18:54	Surface	1	22.6 22.7	22.7	8.4 8.4	8.4	33.5 33.5	33.5	90.5 89.9	90.2	6.4 6.4	6.4	6.4	6.4	1.6 1.7	1.7	1.9	5.1 5.0	5.1	5.5
				Middle	10	22.7 22.7	22.7	8.4 8.4	8.4	33.5 33.6	33.6	90.1 89.7	89.9	6.4 6.4	6.4	6.4		1.7 1.6	1.7		4.9 5.1	5.0	
				Bottom	19	22.7 22.7	22.7	8.4 8.4	8.4	33.6 33.6	33.6	91.6 90.8	91.2	6.5 6.5	6.5	6.5		2.2 2.1	2.2		6.2 6.4	6.3	
C2	Rainy	Calm	17:39	Surface	1	22.7 22.8	22.8	8.3 8.3	8.3	33.3 33.3	33.3	86.6 86.5	86.6	6.2 6.2	6.2	6.2	6.2	1.7 2.0	1.9	2.1	5.6 5.3	5.5	5.9
				Middle	17	22.8 22.8	22.8	8.3 8.3	8.3	33.4 33.4	33.4	86.4 86.9	86.7	6.1 6.2	6.2	6.2		1.9 2.2	2.1		6.4 6.1	6.3	
				Bottom	33	22.8 22.7	22.8	8.3 8.4	8.4	33.5 33.6	33.6	87.9 89.3	88.6	6.2 6.3	6.3	6.3		2.4 2.4	2.4		6.0 6.0	6.0	
G1	Rainy	Calm	18:14	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	92.7 92.4	92.6	6.6 6.6	6.6	6.6	1.1 1.1	1.1	1.1	4.2 4.3	4.3	5.3	
				Middle	3.5	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	92.3 92.3	92.3	6.6 6.6	6.6		6.6	1.0 1.1		1.1	4.7 4.8		4.8
				Bottom	6	22.7 22.6	22.7	8.4 8.4	8.4	33.7 33.7	33.7	91.9 92.1	92.0	6.5 6.6	6.6		6.6	1.2 1.2		1.2	6.8 6.8		6.8
G2	Rainy	Calm	18:03	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.6	33.7	93.1 92.8	93.0	6.6 6.6	6.6	6.6	0.8 0.8	0.8	0.8	5.9 5.9	5.9	4.7	
				Middle	4	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	92.7 92.5	92.6	6.6 6.6	6.6		6.6	0.9 0.8		0.9	4.2 4.1		4.2
				Bottom	7	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	92.7 92.6	92.7	6.6 6.6	6.6		6.6	0.8 0.7		0.8	4.1 4.1		4.1
G3	Rainy	Calm	18:19	Surface	1	22.7 22.7	22.7	8.4 8.4	8.4	33.6 33.7	33.7	90.7 89.9	90.3	6.5 6.4	6.5	6.5	2.2 2.1	2.2	2.2	5.0 5.1	5.1	5.9	
				Middle	3.5	22.7 22.7	22.7	8.4 8.4	8.4	33.8 33.8	33.8	90.6 90.1	90.4	6.4 6.4	6.4		6.4	2.0 2.2		2.1	6.1 6.1		6.1
				Bottom	6	22.7 22.7	22.7	8.4 8.4	8.4	33.8 33.8	33.8	90.5 90.6	90.6	6.4 6.4	6.4		6.4	2.3 2.5		2.4	6.7 6.5		6.6
G4	Rainy	Calm	18:31	Surface	1	22.4 22.4	22.4	8.4 8.4	8.4	33.4 33.4	33.4	87.4 87.3	87.4	6.3 6.2	6.3	6.5	1.0 0.9	1.0	1.5	4.5 4.5	4.5	4.2	
				Middle	4	22.6 22.5	22.6	8.4 8.4	8.4	33.6 33.6	33.6	92.3 91.7	92.0	6.6 6.5	6.6		6.6	1.1 1.1		1.1	5.8 5.9		5.9
				Bottom	7	22.7 22.7	22.7	8.4 8.4	8.4	33.8 33.8	33.8	90.4 90.3	90.4	6.4 6.4	6.4		6.4	2.3 2.3		2.3	2.1 2.1		2.1
M1	Rainy	Calm	18:09	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	92.1 92.2	92.2	6.6 6.6	6.6	6.6	1.2 1.2	1.2	1.4	4.2 4.1	4.2	4.2	
				Middle	3.5	22.6 22.7	22.7	8.4 8.4	8.4	33.7 33.7	33.7	92.3 92.5	92.5	6.6 6.6	6.6		6.6	1.3 1.5		1.4	2.6 2.6		2.6
				Bottom	6	22.7 22.6	22.7	8.4 8.4	8.4	33.7 33.7	33.7	92.4 92.1	92.3	6.6 6.6	6.6		6.6	1.7 1.7		1.7	5.7 5.7		5.7
M2	Rainy	Calm	17:57	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.6	33.6	93.8 93.1	93.5	6.7 6.6	6.7	6.7	0.9 0.8	0.9	1.3	5.5 5.2	5.4	4.5	
				Middle	5.5	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	92.9 92.7	92.8	6.6 6.6	6.6		6.6	0.9 0.8		0.9	3.7 3.7		3.7
				Bottom	10	22.7 22.7	22.7	8.4 8.4	8.4	33.8 33.8	33.8	92.0 92.0	92.0	6.5 6.5	6.5		6.5	2.0 2.0		2.0	4.3 4.2		4.3
M3	Rainy	Calm	18:25	Surface	1	22.7 22.7	22.7	8.4 8.4	8.4	33.6 33.6	33.6	92.2 91.3	91.8	6.6 6.5	6.6	6.6	1.2 1.2	1.2	1.4	5.6 5.7	5.7	6.0	
				Middle	3	22.7 22.7	22.7	8.4 8.4	8.4	33.6 33.7	33.7	91.8 90.8	91.3	6.5 6.5	6.5		6.5	1.2 1.5		1.4	7.0 6.9		7.0
				Bottom	5	22.7 22.7	22.7	8.4 8.4	8.4	33.8 33.7	33.8	89.2 90.4	89.8	6.3 6.4	6.4		6.4	1.5 1.4		1.5	5.2 5.2		5.2
M4	Rainy	Calm	17:46	Surface	1	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.6	33.6	93.9 93.7	93.8	6.7 6.7	6.7	6.7	1.1 1.1	1.1	1.2	4.8 4.7	4.8	4.8	
				Middle	5.5	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	93.6 93.5	93.6	6.7 6.7	6.7		6.7	1.2 1.1		1.2	5.0 4.7		4.9
				Bottom	10	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	93.2 93.3	93.3	6.6 6.6	6.6		6.6	1.3 1.3		1.3	4.7 4.7		4.7
M5	Rainy	Calm	18:47	Surface	1	22.7 22.7	22.7	8.4 8.4	8.4	33.4 33.4	33.4	88.1 87.7	87.9	6.3 6.2	6.3	6.3	2.5 2.3	2.4	2.4	4.1 4.9	4.5	4.8	
				Middle	6.5	22.7 22.7	22.7	8.4 8.4	8.4	33.5 33.5	33.5	88.0 87.7	87.9	6.3 6.2	6.3		6.3	2.5 2.4		2.5	5.2 5.7		5.5
				Bottom	12	22.7 22.7	22.7	8.4 8.4	8.4	33.6 33.6	33.6	88.8 89.1	89.0	6.3 6.3	6.3		6.3	2.4 2.3		2.4	4.9 4.1		4.5
M6	Rainy	Calm	18:36	Surface	-	-	-	-	-	-	-	-	-	-	-	6.4	-	-	1.9	-	-	7.9	
				Middle	2.1	22.6 22.6	22.6	8.4 8.4	8.4	33.5 33.5	33.5	90.1 90.1	90.1	6.4 6.4	6.4		6.4	1.9 1.8		1.9	8.0 7.7		7.9
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 18 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.1 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.4 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.1 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.1 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 18 April 2018**

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity (NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Sunny	Calm	13:54	Surface	1	22.7 22.7	22.7	8.3 8.3	8.3	33.6 33.6	33.6	89.9 88.6	89.3	6.4 6.3	6.4	6.4	1.7 1.7	1.7	1.9	4.4 4.5	4.5	4.8
				Middle	9.5	22.7 22.6	22.7	8.4 8.4	8.4	33.6 33.6	33.6	88.6 88.6	88.6	6.3 6.3	6.3		1.8 1.9	1.9		5.2 5.1	5.2	
				Bottom	18	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.6	33.6	88.2 88.2	88.2	6.3 6.3	6.3		2.0 1.9	2.0		4.8 4.8	4.8	
C2	Sunny	Calm	13:05	Surface	1	22.7 22.7	22.7	8.3 8.3	8.3	33.4 33.4	33.4	87.2 87.2	87.2	6.2 6.2	6.2	6.2	1.8 1.7	1.8	2.2	5.1 5.0	5.1	5.2
				Middle	16.5	22.7 22.7	22.7	8.3 8.3	8.3	33.5 33.5	33.5	86.4 86.7	86.6	6.1 6.2	6.2		2.2 2.0	2.1		5.0 5.0	5.0	
				Bottom	32	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.6	33.6	86.4 87.1	86.8	6.2 6.2	6.2		2.6 2.5	2.6		5.4 5.5	5.5	
G1	Sunny	Calm	13:28	Surface	1	22.7 22.7	22.7	8.3 8.3	8.3	33.4 33.4	33.4	89.4 88.2	88.8	6.4 6.3	6.4	6.4	0.8 0.7	0.8	1.8	5.5 5.5	5.5	3.8
				Middle	4.5	22.6 22.6	22.6	8.3 8.3	8.3	33.6 33.7	33.7	88.4 87.7	88.1	6.3 6.2	6.3		1.9 2.1	2.0		2.6 3.3	2.6	
				Bottom	8	22.6 22.6	22.6	8.4 8.4	8.4	33.8 33.8	33.8	90.3 90.2	90.3	6.4 6.4	6.4		2.5 2.4	2.5		3.3 3.3	3.3	
G2	Sunny	Calm	13:21	Surface	1	22.6 22.7	22.7	8.3 8.3	8.3	33.5 33.5	33.5	88.4 88.3	88.4	6.3 6.3	6.3	6.3	1.0 1.0	1.0	1.3	4.0 4.0	4.0	4.5
				Middle	5	22.6 22.6	22.6	8.3 8.3	8.3	33.6 33.6	33.6	88.5 88.4	88.5	6.3 6.3	6.3		1.1 1.1	1.1		4.8 4.8	4.8	
				Bottom	9	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	90.6 90.2	90.4	6.4 6.4	6.4		1.8 1.8	1.8		4.7 4.6	4.7	
G3	Sunny	Calm	13:32	Surface	1	22.8 22.8	22.8	8.3 8.3	8.3	33.3 33.3	33.3	87.5 85.8	86.7	6.2 6.1	6.2	6.2	1.6 1.6	1.6	1.7	5.1 5.1	5.1	4.0
				Middle	4	22.6 22.6	22.6	8.3 8.3	8.3	33.4 33.5	33.5	86.5 85.4	86.0	6.2 6.1	6.2		1.3 1.5	1.4		4.0 4.1	4.1	
				Bottom	7	22.6 22.6	22.6	8.3 8.3	8.3	33.6 33.6	33.6	85.8 85.3	85.6	6.1 6.1	6.1		1.9 2.0	2.0		2.9 2.9	2.9	
G4	Sunny	Calm	13:39	Surface	1	22.7 22.7	22.7	8.3 8.3	8.3	33.5 33.5	33.5	86.4 86.3	86.4	6.2 6.1	6.2	6.2	1.9 2.0	2.0	1.7	3.3 2.1	3.2	3.6
				Middle	4.5	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.5	33.5	86.4 86.3	86.4	6.2 6.2	6.2		0.7 0.7	0.7		4.4 4.5	4.5	
				Bottom	8	22.6 22.6	22.6	8.3 8.3	8.3	33.7 33.7	33.7	87.0 86.0	86.5	6.2 6.1	6.2		2.5 2.5	2.5		3.2 3.2	3.2	
M1	Sunny	Calm	13:24	Surface	1	22.6 22.7	22.7	8.3 8.3	8.3	33.5 33.5	33.5	88.2 86.3	87.3	6.3 6.1	6.2	6.2	1.4 1.4	1.4	2.2	5.0 5.2	5.1	5.7
				Middle	3	22.6 22.6	22.6	8.3 8.3	8.3	33.6 33.6	33.6	87.6 87.3	87.5	6.2 6.2	6.2		2.3 2.3	2.3		6.6 6.6	6.6	
				Bottom	5	22.6 22.6	22.6	8.4 8.3	8.4	33.7 33.7	33.7	87.8 87.4	87.6	6.2 6.2	6.2		2.9 2.7	2.8		5.4 5.3	5.4	
M2	Sunny	Calm	13:16	Surface	1	22.6 22.6	22.6	8.3 8.4	8.4	33.5 33.5	33.5	89.3 89.5	89.4	6.4 6.4	6.4	6.4	1.6 1.6	1.6	1.9	4.6 4.7	4.7	3.7
				Middle	6	22.6 22.6	22.6	8.4 8.3	8.4	33.6 33.6	33.6	89.8 89.4	89.6	6.4 6.4	6.4		1.5 1.5	1.5		2.6 2.4	2.5	
				Bottom	11	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	90.3 90.0	90.2	6.4 6.4	6.4		2.6 2.4	2.5		3.8 3.8	3.8	
M3	Sunny	Calm	13:35	Surface	1	22.7 22.7	22.7	8.3 8.3	8.3	33.4 33.4	33.4	83.5 84.4	84.0	5.9 6.0	6.0	6.1	1.2 1.3	1.3	1.3	4.9 5.0	5.0	4.3
				Middle	4	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.5	33.5	85.6 84.8	85.2	6.1 6.0	6.1		1.5 1.5	1.5		3.4 3.2	3.3	
				Bottom	7	22.6 22.6	22.6	8.3 8.3	8.3	33.6 33.6	33.6	85.1 83.7	84.4	6.1 6.0	6.1		1.1 1.2	1.2		4.6 4.7	4.7	
M4	Sunny	Calm	13:11	Surface	1	22.6 22.7	22.7	8.3 8.4	8.4	33.6 33.6	33.6	90.5 88.6	89.6	6.4 6.3	6.4	6.4	2.3 2.5	2.4	2.7	4.8 4.7	4.8	4.6
				Middle	5	22.6 22.6	22.6	8.4 8.4	8.4	33.6 33.6	33.6	89.1 88.5	88.8	6.3 6.3	6.3		2.5 2.8	2.7		3.6 3.7	3.7	
				Bottom	9	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	89.6 89.6	89.6	6.4 6.4	6.4		2.7 3.1	2.9		5.2 5.4	5.3	
M5	Sunny	Calm	13:49	Surface	1	22.7 22.7	22.7	8.3 8.4	8.4	33.6 33.6	33.6	87.9 88.8	88.4	6.2 6.3	6.3	6.4	1.9 1.9	1.9	2.0	5.9 5.6	5.8	5.6
				Middle	6	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	89.8 90.5	90.2	6.4 6.4	6.4		1.8 1.8	1.8		5.5 5.5	5.5	
				Bottom	11	22.6 22.6	22.6	8.4 8.4	8.4	33.8 33.8	33.8	90.9 91.1	91.0	6.5 6.5	6.5		2.5 2.2	2.4		5.4 5.3	5.4	
M6	Sunny	Calm	13:44	Surface	-	-	-	-	-	-	-	-	-	-	6.4	-	-	0.9	-	-	6.6	
				Middle	2.1	22.7 22.7	22.7	8.3 8.3	8.3	33.5 33.5	33.5	89.3 89.0	89.2	6.4 6.3		6.4	0.8 0.9		0.9	6.7 6.4		6.6
				Bottom	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 18 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 3.4 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 3.6 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.0 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.5 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.0 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.5 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.3 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.9 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 18 April 2018**

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Sunny	Calm	08:00	Surface	1	22.6 22.6	22.6	8.3 8.4	8.4	33.6 33.5	33.6	86.9 87.1	87.0	6.2 6.2	6.2	6.3	2.2 2.0	2.1	2.4	5.0 4.9	5.0	5.7
				Middle	9	22.6 22.5	22.6	8.4 8.4	8.4	33.7 33.7	33.7	89.9 89.5	89.7	6.4 6.4	6.4		2.3 2.2	2.3		6.0 6.1	6.1	
				Bottom	17	22.6 22.6	22.6	8.4 8.4	8.4	33.9 33.9	33.9	93.4 93.4	93.4	6.6 6.6	6.6		2.8 2.7	2.8		6.2 6.0	6.1	
C2	Sunny	Calm	07:02	Surface	1	22.6 22.6	22.6	8.3 8.3	8.3	33.6 33.4	33.5	89.2 85.9	87.6	6.4 6.1	6.3	6.3	1.3 1.3	1.3	1.4	5.8 5.6	5.7	6.3
				Middle	16.5	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.5	33.5	87.3 86.8	87.1	6.2 6.2	6.2		1.4 1.4	1.4		6.5 6.4	6.5	
				Bottom	32	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.6	33.6	87.1 87.8	87.5	6.2 6.3	6.3		1.5 1.5	1.5		6.8 6.7	6.8	
G1	Sunny	Calm	07:30	Surface	1	22.5 22.5	22.5	8.3 8.3	8.3	33.4 33.4	33.4	86.0 86.1	86.1	6.1 6.2	6.2	6.2	1.3 1.2	1.3	1.4	5.2 5.1	5.2	5.3
				Middle	4.5	22.5 22.5	22.5	8.3 8.3	8.3	33.5 33.5	33.5	85.9 85.8	85.9	6.1 6.1	6.1		1.4 1.3	1.4		6.0 5.9	6.0	
				Bottom	8	22.6 22.6	22.6	8.3 8.3	8.3	33.6 33.6	33.6	87.0 86.9	87.0	6.2 6.2	6.2		1.5 1.5	1.5		4.7 4.5	4.6	
G2	Sunny	Calm	07:20	Surface	1	22.4 22.4	22.4	8.3 8.3	8.3	33.4 33.4	33.4	86.5 86.4	86.5	6.2 6.2	6.2	6.2	1.0 1.0	1.0	1.1	4.5 4.4	4.5	5.0
				Middle	5	22.5 22.5	22.5	8.3 8.3	8.3	33.4 33.5	33.5	86.6 86.8	86.7	6.2 6.2	6.2		1.1 1.3	1.2		4.1 4.1	4.1	
				Bottom	9	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.6	33.6	87.0 87.3	87.2	6.2 6.2	6.2		1.2 1.2	1.2		6.4 6.5	6.5	
G3	Sunny	Calm	07:34	Surface	1	22.5 22.5	22.5	8.3 8.3	8.3	33.3 33.3	33.3	85.3 84.6	85.0	6.1 6.0	6.1	6.1	1.5 1.5	1.5	1.7	5.5 5.4	5.5	6.1
				Middle	4	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.5	33.5	84.7 84.4	84.6	6.0 6.0	6.0		1.7 1.6	1.7		6.8 6.7	6.8	
				Bottom	7	22.6 22.6	22.6	8.3 8.4	8.4	33.6 33.7	33.7	84.8 86.9	85.9	6.0 6.2	6.1		1.9 1.8	1.9		6.1 6.1	6.1	
G4	Sunny	Calm	07:44	Surface	1	22.5 22.5	22.5	8.3 8.3	8.3	33.5 33.5	33.5	85.8 85.4	85.6	6.1 6.1	6.1	6.2	0.9 1.1	1.0	1.3	5.6 5.7	5.7	6.0
				Middle	5	22.5 22.6	22.6	8.3 8.3	8.3	33.6 33.6	33.6	85.2 86.6	85.9	6.1 6.2	6.2		1.0 1.2	1.1		5.5 5.5	5.5	
				Bottom	9	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	84.9 86.9	85.9	6.0 6.2	6.1		1.8 1.5	1.7		6.8 6.6	6.7	
M1	Sunny	Calm	07:25	Surface	1	22.5 22.5	22.5	8.3 8.3	8.3	33.5 33.5	33.5	84.8 84.6	84.7	6.1 6.0	6.1	6.1	1.1 1.2	1.2	1.3	4.0 3.9	4.0	4.4
				Middle	3	22.5 22.5	22.5	8.3 8.3	8.3	33.5 33.5	33.5	84.7 84.5	84.6	6.0 6.0	6.0		1.4 1.3	1.4		4.2 4.2	4.2	
				Bottom	5	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.6	33.6	85.0 86.1	85.6	6.1 6.1	6.1		1.4 1.2	1.3		5.0 5.0	5.0	
M2	Sunny	Calm	07:15	Surface	1	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.5	33.5	88.6 87.3	88.0	6.3 6.2	6.3	6.3	1.4 1.3	1.4	1.4	3.7 3.7	3.7	4.0
				Middle	6	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.5	33.5	87.6 87.2	87.4	6.2 6.2	6.2		1.4 1.4	1.4		2.9 2.7	2.8	
				Bottom	11	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.6	33.6	87.2 86.9	87.1	6.2 6.2	6.2		1.3 1.4	1.4		5.4 5.4	5.4	
M3	Sunny	Calm	07:38	Surface	1	22.5 22.5	22.5	8.3 8.3	8.3	33.3 33.3	33.3	84.4 83.6	84.0	6.0 6.0	6.0	6.0	1.0 1.2	1.1	1.2	3.6 3.5	3.6	5.4
				Middle	4	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.5	33.5	83.3 82.9	83.1	5.9 5.9	5.9		1.1 1.1	1.1		8.6 8.2	8.4	
				Bottom	7	22.6 22.6	22.6	8.3 8.3	8.3	33.7 33.6	33.7	82.1 81.9	82.0	5.8 5.8	5.8		1.3 1.3	1.3		4.3 4.2	4.3	
M4	Sunny	Calm	07:10	Surface	1	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.6	33.6	87.8 88.2	88.0	6.3 6.3	6.3	6.3	1.5 1.7	1.6	2.2	5.1 4.9	5.0	6.1
				Middle	5	22.6 22.6	22.6	8.4 8.3	8.4	33.6 33.6	33.6	88.3 88.2	88.3	6.3 6.3	6.3		2.5 2.5	2.5		6.6 6.9	6.8	
				Bottom	9	22.6 22.6	22.6	8.4 8.4	8.4	33.7 33.7	33.7	88.8 89.6	89.2	6.3 6.4	6.4		2.4 2.4	2.4		6.5 6.7	6.6	
M5	Sunny	Calm	07:54	Surface	1	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.5	33.5	86.5 86.2	86.4	6.2 6.1	6.2	6.2	1.7 1.6	1.7	2.0	4.1 4.1	4.1	5.0
				Middle	6	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.6	33.6	85.8 85.5	85.7	6.1 6.1	6.1		1.9 1.9	1.9		5.9 5.9	5.9	
				Bottom	11	22.5 22.5	22.5	8.4 8.4	8.4	33.7 33.8	33.8	88.9 91.7	90.3	6.3 6.5	6.4		2.4 2.3	2.4		5.1 5.0	5.1	
M6	Sunny	Calm	07:49	Surface	-	-	-	-	-	-	-	-	-	-	6.3	-	-	1.4	-	-	7.8	
				Middle	2.1	22.6 22.6	22.6	8.3 8.3	8.3	33.5 33.5	33.5	87.9 87.6	87.8	6.3 6.2		6.3	1.4 1.4		1.4	7.8 7.8		7.8
				Bottom	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 20 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 5.0 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 5.5 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.7 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.3 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 20 April 2018

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity (NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Cloudy	Calm	15:50	Surface	1	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	88.8 86.7	87.8	6.3 6.2	6.3	6.3	2.6 2.7	2.7	3.5	5.1 5.1	5.1	4.8
				Middle	9	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	86.9 86.8	86.9	6.2 6.2	6.2		2.8 3.0	2.9		4.9 5.0	5.0	
				Bottom	17	22.7 22.7	22.7	7.9 7.9	7.9	33.5 33.5	33.5	88.0 87.6	87.8	6.3 6.2	6.3		4.8 4.9	4.9		4.3 4.3	4.3	
C2	Cloudy	Calm	14:33	Surface	1	22.9 22.9	22.9	7.9 7.9	7.9	33.2 33.2	33.2	87.1 86.0	86.6	6.2 6.1	6.2	6.2	3.1 3.0	3.1	4.3	5.4 5.5	5.5	5.5
				Middle	16.5	22.8 22.8	22.8	7.9 7.9	7.9	33.3 33.4	33.4	85.4 85.5	85.5	6.1 6.1	6.1		5.7 5.7	5.7		5.2 5.3	5.3	
				Bottom	32	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	85.5 85.4	85.5	6.1 6.1	6.1		4.2 4.2	4.2		5.5 5.6	5.6	
G1	Cloudy	Calm	15:10	Surface	1	23.0 23.0	23.0	7.9 7.9	7.9	33.4 33.4	33.4	91.5 90.5	91.0	6.5 6.4	6.5	6.4	1.0 1.0	1.0	1.5	3.5 3.7	3.5	4.2
				Middle	4	22.8 22.8	22.8	7.9 7.9	7.9	33.5 33.5	33.5	88.8 88.8	88.8	6.3 6.3	6.3		1.9 1.7	1.8		2.5 2.8	2.8	
				Bottom	7	22.7 22.7	22.7	7.9 7.9	7.9	33.6 33.6	33.6	87.6 88.2	87.9	6.2 6.3	6.3		1.8 1.8	1.8		6.3 6.2	6.3	
G2	Cloudy	Calm	14:59	Surface	1	22.9 22.9	22.9	7.9 7.9	7.9	33.4 33.4	33.4	92.1 91.3	91.7	6.5 6.5	6.5	6.5	1.2 1.2	1.2	2.3	5.5 5.5	5.5	5.5
				Middle	5	22.8 22.8	22.8	7.9 7.9	7.9	33.5 33.5	33.5	89.4 89.6	89.5	6.4 6.4	6.4		2.5 2.3	2.4		5.3 5.2	5.3	
				Bottom	9	22.7 22.7	22.7	7.9 7.9	7.9	33.6 33.6	33.6	87.9 88.2	88.1	6.3 6.3	6.3		3.2 3.1	3.2		5.6 5.7	5.7	
G3	Cloudy	Calm	15:17	Surface	1	22.9 22.8	22.9	7.9 7.9	7.9	33.4 33.3	33.0	85.7 84.5	85.1	6.1 6.0	6.1	6.1	2.7 2.2	2.5	3.1	4.1 4.2	4.2	4.4
				Middle	4	22.9 22.8	22.9	7.9 7.9	7.9	33.5 33.4	33.5	88.0 83.2	85.6	6.2 5.9	6.1		3.4 3.3	3.4		5.3 5.4	5.4	
				Bottom	7	22.8 22.7	22.8	7.9 7.9	7.9	33.6 33.6	33.6	87.1 85.8	86.5	6.2 6.1	6.2		3.5 3.4	3.5		3.5 3.5	3.5	
G4	Cloudy	Calm	15:29	Surface	1	22.9 22.9	22.9	7.9 7.9	7.9	33.5 33.5	33.5	92.8 91.6	92.2	6.6 6.5	6.6	6.5	1.0 1.1	1.1	2.0	3.2 3.2	3.2	6.5
				Middle	4.5	22.8 22.8	22.8	7.9 7.9	7.9	33.5 33.5	33.5	90.1 89.9	90.0	6.4 6.4	6.4		1.1 1.3	1.2		11.0 11.1	11.1	
				Bottom	8	22.8 22.8	22.8	7.9 7.9	7.9	33.6 33.6	33.6	82.6 85.6	84.1	5.9 6.1	6.0		3.9 3.5	3.7		5.1 5.2	5.2	
M1	Cloudy	Calm	15:05	Surface	1	22.9 22.9	22.9	7.9 7.9	7.9	33.4 33.4	33.4	91.6 89.3	90.5	6.5 6.3	6.4	6.4	1.0 1.2	1.1	1.4	4.3 4.3	4.3	4.7
				Middle	3	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	88.7 88.8	88.8	6.3 6.3	6.3		1.5 1.5	1.5		4.8 4.8	4.8	
				Bottom	5	22.8 22.8	22.8	7.9 7.9	7.9	33.5 33.5	33.5	88.1 88.5	88.3	6.3 6.3	6.3		1.7 1.7	1.7		4.8 4.9	4.9	
M2	Cloudy	Calm	14:52	Surface	1	22.9 22.9	22.9	7.9 7.9	7.9	33.4 33.4	33.4	93.7 91.9	92.8	6.7 6.5	6.6	6.6	1.1 1.1	1.1	2.1	4.6 4.7	4.7	4.9
				Middle	6	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	91.3 91.2	91.3	6.5 6.5	6.5		1.2 1.2	1.2		3.9 4.0	4.0	
				Bottom	11	22.7 22.7	22.7	7.9 7.9	7.9	33.6 33.5	33.6	86.6 88.2	87.4	6.2 6.3	6.3		4.0 4.0	4.0		5.9 5.8	5.9	
M3	Cloudy	Calm	15:23	Surface	1	22.8 22.8	22.8	7.9 7.9	7.9	33.3 33.3	33.3	78.7 79.3	79.0	5.6 5.6	5.6	6.0	2.0 2.1	2.1	2.5	4.8 4.8	4.8	5.3
				Middle	4	22.9 22.9	22.9	7.9 7.9	7.9	33.5 33.5	33.5	89.9 89.4	89.7	6.4 6.3	6.4		1.0 1.2	1.1		5.2 5.4	5.3	
				Bottom	7	22.7 22.7	22.7	7.9 7.9	7.9	33.6 33.6	33.6	85.2 83.9	84.6	6.1 6.0	6.1		4.1 4.7	4.4		5.9 5.8	5.9	
M4	Cloudy	Calm	14:43	Surface	1	22.7 22.7	22.7	7.9 7.9	7.9	33.5 33.5	33.5	89.6 88.8	89.2	6.4 6.3	6.4	6.4	2.4 2.6	2.5	2.5	4.8 4.9	4.9	4.9
				Middle	5	22.7 22.7	22.7	7.9 7.9	7.9	33.5 33.5	33.5	88.8 88.4	88.6	6.3 6.3	6.3		2.4 2.6	2.5		4.6 4.5	4.6	
				Bottom	9	22.7 22.7	22.7	7.9 7.9	7.9	33.5 33.5	33.5	88.4 88.2	88.3	6.3 6.3	6.3		2.5 2.6	2.6		5.3 5.2	5.3	
M5	Cloudy	Calm	15:42	Surface	1	22.8 22.9	22.9	8.0 8.0	8.0	33.5 33.5	33.5	93.6 92.3	93.0	6.6 6.5	6.6	6.6	1.5 1.5	1.5	2.1	4.5 4.6	4.6	3.7
				Middle	5.5	22.8 22.8	22.8	8.0 8.0	8.0	33.5 33.5	33.5	91.1 90.9	91.0	6.5 6.5	6.5		2.0 1.9	2.0		3.8 3.9	3.9	
				Bottom	10	22.7 22.7	22.7	8.0 8.0	8.0	33.6 33.6	33.6	92.4 91.4	91.9	6.6 6.5	6.6		2.8 2.6	2.7		2.5 2.5	2.5	
M6	Cloudy	Calm	15:36	Surface	-	-	-	-	-	-	-	-	-	-	-	6.5	-	-	1.1	-	-	4.2
				Middle	1.4	22.9 22.9	22.9	7.9 7.9	7.9	33.5 33.5	33.5	92.0 91.4	91.7	6.5 6.5	6.5		1.1 1.0	1.1		4.2 4.1	4.2	
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-	

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 20 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 4.1 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 4.4 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.2 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.2 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 8.2 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 8.8 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 20 April 2018**

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Cloudy	Calm	10:03	Surface	1	22.7 22.7	22.7	8.0 8.0	8.0	33.5 33.5	33.5	92.4 92.1	92.3	6.6 6.6	6.6	6.7	1.5 1.6	1.6	2.4	5.4 5.5	5.5	6.1
				Middle	9	22.6 22.6	22.6	8.0 8.0	8.0	33.6 33.6	33.6	94.2 94.3	94.3	6.7 6.7	6.7		2.0 2.1	2.1		5.8 6.0	5.9	
				Bottom	17	22.6 22.6	22.6	8.0 8.0	8.0	33.6 33.6	33.6	94.5 94.5	94.5	6.7 6.7	6.7		3.4 3.4	3.4		6.8 6.8	6.8	
C2	Cloudy	Calm	08:47	Surface	1	22.8 22.8	22.8	7.8 7.9	7.9	33.3 33.3	33.3	87.6 87.3	87.5	6.2 6.2	6.2	6.2	1.5 1.5	1.5	2.3	5.8 5.8	5.8	5.8
				Middle	16.5	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	86.6 85.1	85.9	6.2 6.1	6.2		2.0 2.0	2.0		5.8 5.9	5.9	
				Bottom	32	22.7 22.7	22.7	7.9 7.9	7.9	33.5 33.6	33.6	87.7 89.6	88.7	6.2 6.4	6.3		3.3 3.3	3.3		5.7 5.7	5.7	
G1	Cloudy	Calm	09:25	Surface	1	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	90.2 88.8	89.5	6.4 6.3	6.4	6.4	1.1 1.0	1.1	1.2	5.6 5.6	5.6	5.7
				Middle	4	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	88.7 88.3	88.5	6.3 6.3	6.3		1.1 1.2	1.2		5.4 5.5	5.5	
				Bottom	7	22.8 22.8	22.8	7.9 7.9	7.9	33.5 33.5	33.5	88.5 88.5	88.5	6.3 6.3	6.3		1.2 1.1	1.2		5.9 6.0	6.0	
G2	Cloudy	Calm	09:09	Surface	1	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	90.4 89.4	89.9	6.4 6.4	6.4	6.4	1.1 1.1	1.1	1.4	4.2 4.3	4.3	5.2
				Middle	5	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	88.8 88.5	88.7	6.3 6.3	6.3		1.2 1.2	1.2		8.0 8.0	8.0	
				Bottom	9	22.7 22.7	22.7	7.9 8.0	8.0	33.6 33.6	33.6	89.2 89.3	89.3	6.3 6.4	6.4		1.7 1.8	1.8		3.4 3.4	3.4	
G3	Cloudy	Calm	09:31	Surface	1	22.8 22.8	22.8	7.9 7.9	7.9	33.2 33.3	33.3	89.2 87.1	88.2	6.3 6.2	6.3	6.2	1.0 1.0	1.0	1.5	3.2 3.3	3.3	3.2
				Middle	4	22.8 22.8	22.8	7.9 7.9	7.9	33.6 33.5	33.6	85.4 86.2	85.8	6.1 6.1	6.1		1.4 1.3	1.4		3.9 4.0	4.0	
				Bottom	7	22.7 22.7	22.7	7.9 7.9	7.9	33.6 33.6	33.6	86.9 86.9	86.9	6.2 6.2	6.2		2.1 2.0	2.1		2.2 2.3	2.3	
G4	Cloudy	Calm	09:42	Surface	1	22.8 22.8	22.8	7.9 7.9	7.9	33.5 33.5	33.5	90.8 89.9	90.4	6.5 6.4	6.5	6.5	1.1 1.1	1.1	1.3	2.5 2.5	2.5	3.9
				Middle	4.5	22.8 22.7	22.8	7.9 8.0	8.0	33.5 33.5	33.5	89.4 90.3	89.9	6.4 6.4	6.4		1.1 1.2	1.2		4.3 4.2	4.3	
				Bottom	8	22.7 22.7	22.7	8.0 8.0	8.0	33.6 33.6	33.6	89.8 87.9	88.9	6.4 6.3	6.4		1.4 1.7	1.6		5.0 5.0	5.0	
M1	Cloudy	Calm	09:17	Surface	1	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	89.9 88.5	89.2	6.4 6.3	6.4	6.4	1.1 1.2	1.2	1.2	5.2 5.2	5.2	5.3
				Middle	3	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	88.6 88.2	88.4	6.3 6.3	6.3		1.1 1.1	1.2		4.8 5.0	4.9	
				Bottom	5	22.8 22.8	22.8	7.9 7.9	7.9	33.5 33.5	33.5	88.3 87.7	88.0	6.3 6.2	6.3		1.2 1.3	1.3		5.7 5.6	5.7	
M2	Cloudy	Calm	09:03	Surface	1	22.7 22.7	22.7	7.9 7.9	7.9	33.4 33.4	33.4	89.9 89.4	89.7	6.4 6.4	6.4	6.4	1.2 1.2	1.2	1.7	4.9 4.8	4.9	4.9
				Middle	6	22.7 22.7	22.7	7.9 7.9	7.9	33.4 33.4	33.4	88.9 88.8	88.9	6.3 6.3	6.3		1.3 1.2	1.3		5.0 4.8	4.9	
				Bottom	11	22.7 22.7	22.7	8.0 7.9	8.0	33.6 33.6	33.6	89.9 89.4	89.7	6.4 6.4	6.4		2.8 2.5	2.7		4.9 4.8	4.9	
M3	Cloudy	Calm	09:36	Surface	1	22.8 22.8	22.8	7.9 7.9	7.9	33.3 33.3	33.3	88.9 88.5	88.7	6.3 6.3	6.3	6.3	1.1 1.1	1.1	1.4	5.4 5.4	5.4	5.0
				Middle	4	22.9 22.9	22.9	7.9 7.9	7.9	33.5 33.5	33.5	87.7 87.4	87.6	6.2 6.2	6.2		1.1 1.2	1.2		3.3 3.2	3.3	
				Bottom	7	22.7 22.7	22.7	7.9 7.9	7.9	33.6 33.6	33.6	87.6 87.6	87.6	6.2 6.2	6.2		2.0 1.9	2.0		6.4 6.4	6.4	
M4	Cloudy	Calm	08:55	Surface	1	22.7 22.7	22.7	7.9 7.9	7.9	33.5 33.5	33.5	90.3 89.6	90.0	6.4 6.4	6.4	6.4	1.3 1.3	1.3	1.3	5.6 5.4	5.5	4.2
				Middle	5	22.7 22.7	22.7	7.9 7.9	7.9	33.5 33.5	33.5	89.3 89.2	89.3	6.4 6.3	6.4		1.4 1.2	1.3		2.9 2.9	2.9	
				Bottom	9	22.7 22.7	22.7	7.9 7.9	7.9	33.5 33.5	33.5	88.8 88.8	88.8	6.3 6.3	6.3		1.5 1.3	1.4		4.3 4.3	4.3	
M5	Cloudy	Calm	09:56	Surface	1	22.8 22.8	22.8	7.9 7.9	7.9	33.4 33.4	33.4	89.5 89.4	89.5	6.4 6.4	6.4	6.4	1.4 1.3	1.4	1.9	3.9 3.9	3.9	5.1
				Middle	5.5	22.7 22.7	22.7	7.9 7.9	7.9	33.5 33.5	33.5	89.4 89.2	89.3	6.4 6.3	6.4		2.0 1.9	2.0		7.3 7.4	7.4	
				Bottom	10	22.7 22.7	22.7	8.0 8.0	8.0	33.6 33.6	33.6	90.9 91.7	91.3	6.5 6.5	6.5		2.1 2.4	2.3		3.9 4.1	4.0	
M6	Cloudy	Calm	09:49	Surface	-	-	-	-	-	-	-	-	-	-	6.4	-	-	1.2	-	-	2.5	
				Middle	1.5	22.8 22.8	22.8	7.9 7.9	7.9	33.5 33.5	33.5	90.1 90.0	90.1	6.4 6.4		6.4	1.1 1.2		1.2	2.5 2.5		2.5
				Bottom	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 23 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 4.0 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 4.3 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.9 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.4 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 5.9 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.4 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.9 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 8.6 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 23 April 2018

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Fine	Moderate	19:15	Surface	1	23.6 23.6	23.6	8.4 8.4	8.4	33.2 33.2	33.2	89.2 89.0	89.1	6.3 6.2	6.3	6.3	2.1 2.1	2.1	2.9	4.6 4.6	4.6	3.9
				Middle	10	22.9 22.8	22.9	8.4 8.4	8.4	33.7 33.8	33.8	88.3 89.2	88.8	6.2 6.3	6.3		3.2 3.4	3.3		3.9 3.8	3.9	
				Bottom	19	22.8 22.8	22.8	8.5 8.5	8.5	33.9 33.9	33.9	91.6 91.7	91.7	6.5 6.5	6.5		3.3 3.2	3.3		3.1 3.0	3.1	
C2	Fine	Moderate	17:31	Surface	1	23.7 23.7	23.7	8.4 8.4	8.4	33.2 33.2	33.2	90.9 90.7	90.8	6.4 6.3	6.4	6.4	1.1 1.1	1.1	2.4	4.8 4.9	4.9	5.4
				Middle	17	22.9 22.9	22.9	8.5 8.5	8.5	33.7 33.8	33.8	88.5 88.7	88.6	6.3 6.3	6.3		2.6 2.7	2.7		4.6 4.7	4.7	
				Bottom	33	22.8 22.8	22.8	8.6 8.6	8.6	33.9 33.9	33.9	91.5 91.7	91.6	6.5 6.5	6.5		3.3 3.2	3.3		6.5 6.6	6.6	
G1	Fine	Moderate	18:19	Surface	1	24.1 24.1	24.1	8.4 8.4	8.4	33.6 33.6	33.6	101.9 102.2	102.1	7.1 7.1	7.1	7.1	1.2 1.3	1.3	1.4	3.6 3.7	3.7	4.5
				Middle	4	24.0 24.0	24.0	8.4 8.4	8.4	33.6 33.6	33.6	101.9 101.6	101.8	7.1 7.1	7.1		1.3 1.3	1.3		4.9 4.7	4.8	
				Bottom	7	23.1 23.0	23.1	8.4 8.4	8.4	33.8 33.8	33.8	96.2 96.2	96.2	6.8 6.8	6.8		1.5 1.5	1.5		5.1 5.0	5.1	
G2	Fine	Moderate	18:00	Surface	1	24.0 24.0	24.0	8.4 8.4	8.4	33.6 33.6	33.6	100.7 100.7	100.7	7.0 7.0	7.0	7.0	1.4 1.4	1.4	1.5	5.0 5.1	5.1	5.9
				Middle	5	24.0 24.0	24.0	8.4 8.4	8.4	33.6 33.6	33.6	100.8 100.8	100.8	7.0 7.0	7.0		1.5 1.4	1.5		8.5 8.4	8.5	
				Bottom	9	22.9 22.9	22.9	8.5 8.5	8.5	33.8 33.8	33.8	95.7 95.6	95.7	6.8 6.8	6.8		1.5 1.5	1.5		4.1 4.0	4.1	
G3	Fine	Moderate	18:28	Surface	1	24.2 24.2	24.2	8.4 8.4	8.4	33.6 33.6	33.6	99.7 100.1	99.9	6.9 6.9	6.9	7.0	1.4 1.4	1.4	1.8	3.1 3.1	3.1	4.1
				Middle	4	23.7 23.8	23.8	8.4 8.4	8.4	33.6 33.6	33.6	100.1 100.3	100.2	7.0 7.0	7.0		1.5 1.5	1.5		4.1 4.2	4.2	
				Bottom	7	23.1 22.9	23.0	8.4 8.4	8.4	33.7 33.8	33.8	94.2 93.7	94.0	6.6 6.6	6.6		2.7 2.3	2.5		5.0 5.1	5.1	
G4	Fine	Moderate	18:45	Surface	1	24.2 24.2	24.2	8.4 8.4	8.4	33.6 33.6	33.6	100.6 100.7	100.7	7.0 7.0	7.0	7.0	1.4 1.4	1.4	1.9	3.6 3.5	3.6	3.8
				Middle	4	23.0 23.0	23.0	8.4 8.4	8.4	33.7 33.7	33.7	97.3 96.9	97.1	6.9 6.8	6.9		1.8 1.9	1.9		3.6 3.6	3.6	
				Bottom	7	22.8 22.8	22.8	8.5 8.5	8.5	34.0 34.0	34.0	90.2 90.8	90.5	6.4 6.4	6.4		2.4 2.5	2.5		4.1 4.0	4.1	
M1	Fine	Moderate	18:10	Surface	1	24.0 24.0	24.0	8.4 8.4	8.4	33.6 33.6	33.6	100.5 100.6	100.6	7.0 7.0	7.0	7.0	1.3 1.1	1.2	1.3	5.4 5.4	5.4	4.5
				Middle	3	24.0 24.0	24.0	8.4 8.4	8.4	33.6 33.6	33.6	100.6 100.5	100.6	7.0 7.0	7.0		1.3 1.3	1.3		3.9 3.9	3.9	
				Bottom	5	23.9 23.9	23.9	8.4 8.4	8.4	33.6 33.6	33.6	100.4 100.3	100.4	7.0 7.0	7.0		1.3 1.3	1.3		4.1 4.1	4.1	
M2	Fine	Moderate	17:52	Surface	1	23.9 23.9	23.9	8.4 8.4	8.4	33.6 33.6	33.6	100.7 100.7	100.7	7.0 7.0	7.0	7.0	1.3 1.3	1.3	1.3	5.6 5.5	5.6	4.7
				Middle	6	23.9 23.9	23.9	8.4 8.4	8.4	33.6 33.6	33.6	100.6 100.5	100.6	7.0 7.0	7.0		1.3 1.3	1.3		3.9 4.0	4.0	
				Bottom	11	23.2 23.0	23.1	8.4 8.4	8.4	33.7 33.8	33.8	95.9 95.8	95.9	6.7 6.8	6.8		1.3 1.3	1.3		4.5 4.4	4.5	
M3	Fine	Moderate	18:37	Surface	1	24.1 24.2	24.2	8.4 8.4	8.4	33.6 33.6	33.6	100.5 100.5	100.5	7.0 7.0	7.0	7.0	2.2 2.2	2.2	1.7	3.6 3.6	3.6	6.0
				Middle	4	24.1 24.0	24.1	8.4 8.4	8.4	33.6 33.6	33.6	100.4 100.5	100.5	7.0 7.0	7.0		1.4 1.4	1.4		7.5 7.6	7.6	
				Bottom	7	23.6 23.4	23.5	8.4 8.4	8.4	33.6 33.6	33.6	99.7 99.0	99.4	7.0 6.9	7.0		1.4 1.4	1.4		6.8 6.7	6.8	
M4	Fine	Moderate	17:42	Surface	1	23.6 23.6	23.6	8.4 8.4	8.4	33.2 33.2	33.2	89.6 89.4	89.5	6.3 6.3	6.3	6.3	1.9 2.0	2.0	2.4	4.6 4.6	4.6	3.8
				Middle	5	23.4 23.4	23.4	8.4 8.4	8.4	33.3 33.3	33.3	88.7 88.6	88.7	6.2 6.2	6.2		2.2 2.3	2.3		3.8 3.6	3.7	
				Bottom	9	23.2 23.0	23.1	8.4 8.4	8.4	33.5 33.6	33.6	88.4 88.1	88.3	6.2 6.2	6.2		2.9 2.8	2.9		3.0 2.9	3.0	
M5	Fine	Moderate	19:06	Surface	1	23.6 23.6	23.6	8.4 8.4	8.4	33.2 33.2	33.2	89.5 89.3	89.4	6.3 6.3	6.3	6.3	2.0 1.9	2.0	2.5	5.6 5.6	5.6	5.7
				Middle	5.5	23.5 23.3	23.4	8.4 8.4	8.4	33.3 33.4	33.4	88.6 88.3	88.5	6.2 6.2	6.2		2.2 2.3	2.3		5.1 5.2	5.2	
				Bottom	10	23.1 22.9	23.0	8.4 8.4	8.4	33.5 33.7	33.6	88.2 88.2	88.2	6.2 6.2	6.2		2.9 3.4	3.2		6.3 6.5	6.4	
M6	Fine	Moderate	18:54	Surface	-	-	-	-	-	-	-	-	-	-	-	7.0	-	-	1.4	-	-	6.0
				Middle	2.1	24.1 24.1	24.1	8.4 8.4	8.4	33.6 33.6	33.6	100.7 100.7	100.7	7.0 7.0	7.0		1.4 1.4	1.4		5.9 6.0	6.0	
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-	

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 23 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 2.5 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 2.7 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.8 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.4 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.8 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.4 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.1 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.6 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 23 April 2018

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Fine	Moderate	12:42	Surface	1	23.2 23.2	23.2	8.6 8.6	8.6	33.4 33.4	33.4	87.9 87.6	87.8	6.2 6.2	6.2	6.4	1.6 1.5	1.6	1.8	5.8 5.6	5.7	4.9
				Middle	9	23.0 22.9	23.0	8.6 8.6	8.6	33.8 33.8	33.8	91.1 91.9	91.5	6.4 6.5	6.5	6.4 6.5	1.8	1.8		3.8 3.7	3.8	
				Bottom	17	22.7 22.7	22.7	8.6 8.6	8.6	33.9 33.9	33.9	92.9 92.9	92.9	6.6 6.6	6.6	6.6 6.6	2.1 2.1	2.1		5.1 5.1	5.1	
C2	Fine	Moderate	11:00	Surface	1	23.2 23.2	23.2	8.4 8.4	8.4	33.4 33.4	33.4	87.5 87.4	87.5	6.2 6.2	6.2	6.4	1.2 1.2	1.2	1.3	3.8 3.7	3.8	4.3
				Middle	16.5	22.9 22.9	22.9	8.4 8.4	8.4	33.8 33.8	33.8	91.3 91.6	91.5	6.5 6.5	6.5	6.5 6.5	1.3 1.3	1.3		4.8 4.8	4.8	
				Bottom	32	22.7 22.7	22.7	8.2 8.2	8.2	33.9 33.9	33.9	92.7 92.8	92.8	6.6 6.6	6.6	6.6 6.6	1.5 1.5	1.5		4.2 4.3	4.3	
G1	Fine	Moderate	11:43	Surface	1	23.5 23.5	23.5	8.4 8.4	8.4	33.5 33.5	33.5	93.9 93.9	93.9	6.6 6.6	6.6	6.6	1.5 1.5	1.5	1.8	5.2 5.2	5.2	6.3
				Middle	4	23.2 23.2	23.2	8.5 8.5	8.5	33.6 33.6	33.6	93.1 93.3	93.2	6.6 6.6	6.6	6.6 6.6	1.9 1.8	1.9		9.7 9.7	9.7	
				Bottom	7	23.1 23.0	23.1	8.5 8.5	8.5	33.6 33.7	33.7	92.6 92.2	92.4	6.5 6.5	6.5	6.5 6.5	1.9 2.0	2.0		4.1 4.1	4.1	
G2	Fine	Moderate	11:27	Surface	1	23.3 23.3	23.3	8.4 8.4	8.4	33.6 33.6	33.6	93.0 93.1	93.1	6.5 6.5	6.5	6.6	0.8 0.8	0.8	1.0	3.9 4.1	4.0	4.2
				Middle	5	22.9 22.9	22.9	8.4 8.5	8.5	33.7 33.8	33.8	92.4 92.6	92.5	6.5 6.6	6.6	6.6 6.6	1.1 1.1	1.1		3.5 3.5	3.5	
				Bottom	9	22.9 22.9	22.9	8.5 8.5	8.5	33.8 33.8	33.8	92.9 93.0	93.0	6.6 6.6	6.6	6.6 6.6	1.1 1.2	1.2		5.1 4.8	5.0	
G3	Fine	Moderate	12:01	Surface	1	23.5 23.5	23.5	8.4 8.4	8.4	33.5 33.5	33.5	93.0 93.0	93.0	6.5 6.5	6.5	6.5	1.5 1.5	1.5	1.9	5.5 5.6	5.6	5.2
				Middle	4	23.4 23.4	23.4	8.4 8.4	8.4	33.5 33.5	33.5	92.9 92.9	92.9	6.5 6.5	6.5	6.5 6.5	1.6 1.6	1.6		5.5 5.6	5.6	
				Bottom	7	22.9 22.9	22.9	8.5 8.5	8.5	33.8 33.8	33.8	92.3 92.5	92.4	6.5 6.5	6.5	6.5 6.5	2.6 2.5	2.6		4.3 4.2	4.3	
G4	Fine	Moderate	12:17	Surface	1	23.6 23.6	23.6	8.4 8.4	8.4	33.5 33.5	33.5	93.4 93.0	93.2	6.5 6.5	6.5	6.6	1.6 1.6	1.6	1.7	5.0 5.0	5.0	5.0
				Middle	4	23.0 23.0	23.0	8.5 8.5	8.5	33.7 33.7	33.7	93.4 93.6	93.5	6.6 6.6	6.6	6.6 6.6	1.7 1.7	1.7		4.3 4.5	4.4	
				Bottom	7	22.9 22.9	22.9	8.5 8.5	8.5	33.8 33.8	33.8	93.6 93.7	93.7	6.6 6.6	6.6	6.6 6.6	1.7 1.7	1.7		5.5 5.5	5.5	
M1	Fine	Moderate	11:36	Surface	1	23.5 23.5	23.5	8.4 8.4	8.4	33.6 33.6	33.6	93.2 93.1	93.2	6.5 6.5	6.5	6.5	1.4 1.4	1.4	1.6	3.5 3.5	3.5	4.8
				Middle	3	23.1 23.0	23.1	8.4 8.4	8.4	33.7 33.7	33.7	92.2 92.2	92.2	6.5 6.5	6.5	6.5 6.5	1.5 1.6	1.6		5.1 4.9	5.0	
				Bottom	5	22.9 22.9	22.9	8.5 8.5	8.5	33.8 33.8	33.8	92.6 92.6	92.7	6.6 6.6	6.6	6.6 6.6	1.8 1.8	1.8		5.9 5.6	5.8	
M2	Fine	Moderate	11:18	Surface	1	23.2 23.3	23.3	8.5 8.5	8.5	33.6 33.6	33.6	93.5 93.3	93.4	6.6 6.6	6.6	6.6	1.3 1.4	1.4	1.7	4.9 5.1	5.0	4.8
				Middle	6	23.0 22.9	23.0	8.5 8.5	8.5	33.7 33.8	33.8	92.7 92.7	92.7	6.6 6.6	6.6	6.6 6.6	1.6 1.7	1.7		4.9 4.8	4.9	
				Bottom	11	22.8 22.8	22.8	8.5 8.5	8.5	33.8 33.9	33.9	93.2 93.4	93.3	6.6 6.6	6.6	6.6 6.6	1.9 2.0	2.0		4.5 4.5	4.5	
M3	Fine	Moderate	12:09	Surface	1	23.6 23.6	23.6	8.4 8.4	8.4	33.5 33.5	33.5	93.4 93.2	93.3	6.5 6.5	6.5	6.5	1.4 1.4	1.4	1.8	5.0 5.0	5.0	5.1
				Middle	4	23.5 23.4	23.5	8.4 8.4	8.4	33.5 33.6	33.6	92.9 92.9	92.9	6.5 6.5	6.5	6.5 6.5	1.6 1.6	1.6		5.4 5.3	5.4	
				Bottom	7	22.9 23.0	23.0	8.4 8.4	8.4	33.8 33.8	33.8	91.8 91.8	91.8	6.5 6.5	6.5	6.5 6.5	2.3 2.3	2.3		5.0 5.0	5.0	
M4	Fine	Moderate	11:10	Surface	1	23.1 23.1	23.1	8.5 8.5	8.5	33.6 33.6	33.6	93.1 93.1	93.1	6.6 6.6	6.6	6.6	1.3 1.3	1.3	1.8	5.7 5.8	5.8	4.4
				Middle	5	23.0 22.9	23.0	8.5 8.5	8.5	33.7 33.8	33.8	92.8 92.8	92.8	6.6 6.6	6.6	6.6 6.6	1.6 1.7	1.7		4.5 4.4	4.5	
				Bottom	9	22.8 22.8	22.8	8.5 8.5	8.5	33.9 33.9	33.9	93.3 93.4	93.4	6.6 6.6	6.6	6.6 6.6	2.2 2.7	2.5		3.0 3.0	3.0	
M5	Fine	Moderate	12:33	Surface	1	23.6 23.4	23.5	8.4 8.4	8.4	33.5 33.5	33.5	93.7 93.1	93.4	6.6 6.5	6.6	6.6	1.3 1.4	1.4	1.9	5.3 5.4	5.4	5.1
				Middle	5.5	23.2 23.1	23.2	8.4 8.4	8.4	33.6 33.6	33.6	92.7 92.7	92.7	6.5 6.5	6.5	6.5 6.5	1.9 1.8	1.9		5.6 5.4	5.5	
				Bottom	10	23.0 22.9	23.0	8.5 8.5	8.5	33.7 33.8	33.8	92.5 92.4	92.5	6.5 6.5	6.5	6.5 6.5	2.2 2.4	2.3		4.3 4.2	4.3	
M6	Fine	Moderate	12:25	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	1.4	-	-	3.4
				Middle	2.1	23.5 23.6	23.6	8.4 8.4	8.4	33.5 33.5	33.5	93.6 93.5	93.6	6.6 6.6	6.6	6.6 6.6	1.4 1.3	1.4		3.4 3.4	3.4	
				Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-	-	

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 25 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 6.0 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 6.5 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.2 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.7 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 7.3 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 25 April 2018

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Cloudy	Calm	10:20	Surface	1	23.2 23.2	23.2	8.5 8.5	8.5	33.5 33.5	33.5	90.9 90.7	90.8	6.4 6.4	6.4	6.5	0.9 0.8	0.9	2.7	5.2 5.2	5.2	4.7
				Middle	10	23.2 23.2	23.2	8.5 8.5	8.5	33.6 33.6	33.6	91.7 91.5	91.6	6.5 6.5	6.5		1.4 1.5	1.5		4.4 4.3	4.4	
				Bottom	19	22.9 22.9	22.9	8.6 8.6	8.6	34.1 34.1	34.1	91.2 91.2	91.2	6.4 6.4	6.4		5.5 5.6	5.6		4.5 4.4	4.5	
C2	Cloudy	Calm	09:22	Surface	1	23.3 23.3	23.3	8.5 8.5	8.5	33.4 33.3	33.4	87.4 87.2	87.3	6.2 6.1	6.2	6.4	1.7 1.7	1.7	3.4	5.5 5.4	5.5	5.9
				Middle	17	22.9 22.9	22.9	8.6 8.6	8.6	34.1 34.1	34.1	91.5 91.5	91.5	6.5 6.5	6.5		3.4 3.5	3.5		6.8 6.6	6.7	
				Bottom	33	22.8 22.8	22.8	8.6 8.6	8.6	34.1 34.2	34.2	91.7 91.8	91.8	6.5 6.5	6.5		5.1 4.8	5.0		5.5 5.6	5.6	
G1	Cloudy	Calm	09:50	Surface	1	23.2 23.2	23.2	8.5 8.5	8.5	33.7 33.7	33.7	92.0 91.7	91.9	6.5 6.5	6.5	6.5	1.1 1.1	1.1	1.4	2.9 2.9	2.9	4.9
				Middle	4	23.1 23.1	23.1	8.5 8.5	8.5	33.8 33.8	33.8	91.0 90.8	90.9	6.4 6.4	6.4		1.3 1.2	1.3		6.4 6.7	6.6	
				Bottom	7	23.0 23.0	23.0	8.5 8.5	8.5	33.9 33.9	33.9	91.2 90.7	91.0	6.4 6.4	6.4		1.7 2.1	1.9		5.1 5.4	5.3	
G2	Cloudy	Calm	09:41	Surface	1	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.7	33.7	92.0 91.9	92.0	6.5 6.5	6.5	6.6	1.2 1.3	1.3	1.7	3.5 3.6	3.6	5.4
				Middle	5	23.1 23.1	23.1	8.5 8.5	8.5	33.8 33.7	33.8	92.9 93.0	93.0	6.6 6.6	6.6		1.2 1.3	1.3		6.1 6.2	6.2	
				Bottom	9	23.0 23.0	23.0	8.5 8.5	8.5	34.0 34.0	34.0	91.9 91.7	91.8	6.5 6.5	6.5		2.5 2.5	2.5		6.6 6.4	6.5	
G3	Cloudy	Calm	09:55	Surface	1	23.2 23.3	23.3	8.5 8.5	8.5	33.5 33.5	33.5	90.8 90.8	90.8	6.4 6.4	6.4	6.4	1.3 1.3	1.3	2.2	5.0 4.7	4.9	6.7
				Middle	4	23.1 23.0	23.1	8.5 8.5	8.5	33.9 33.9	33.9	89.3 88.1	88.7	6.3 6.2	6.3		2.1 2.1	2.1		8.7 8.7	8.7	
				Bottom	7	23.0 23.0	23.0	8.5 8.5	8.5	34.0 34.0	34.0	90.5 90.3	90.4	6.4 6.4	6.4		2.9 3.3	3.1		6.6 6.5	6.6	
G4	Cloudy	Calm	10:04	Surface	1	23.2 23.2	23.2	8.5 8.5	8.5	33.7 33.6	33.7	89.7 89.5	89.6	6.3 6.3	6.3	6.4	2.1 1.8	2.0	2.4	4.2 4.1	4.2	4.7
				Middle	4	23.0 23.0	23.0	8.5 8.5	8.5	34.0 34.0	34.0	92.7 92.1	92.4	6.5 6.5	6.5		2.2 2.0	2.1		4.8 5.0	4.9	
				Bottom	7	23.0 23.0	23.0	8.5 8.6	8.6	34.0 34.0	34.0	92.1 92.5	92.3	6.5 6.5	6.5		3.4 2.9	3.2		4.9 5.0	5.0	
M1	Cloudy	Calm	09:46	Surface	1	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.7	33.7	90.8 89.4	90.1	6.4 6.3	6.4	6.4	1.9 1.7	1.8	1.9	3.0 3.0	3.0	4.0
				Middle	3	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.7	33.7	89.7 89.6	89.7	6.3 6.3	6.3		1.9 1.8	1.9		3.9 3.7	3.8	
				Bottom	5	23.1 23.1	23.1	8.5 8.5	8.5	33.8 33.7	33.8	89.5 89.5	89.5	6.3 6.3	6.3		2.0 2.0	2.0		5.3 5.3	5.3	
M2	Cloudy	Calm	09:35	Surface	1	23.2 23.2	23.2	8.5 8.5	8.5	33.5 33.6	33.6	91.2 91.3	91.3	6.4 6.4	6.4	6.5	1.3 1.4	1.4	2.4	4.1 3.9	4.0	3.9
				Middle	5.5	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.7	33.7	91.2 91.5	91.4	6.4 6.5	6.5		1.7 1.7	1.7		3.6 3.5	3.6	
				Bottom	10	22.9 23.0	23.0	8.5 8.5	8.5	34.1 34.0	34.1	90.4 90.6	90.5	6.4 6.4	6.4		4.1 4.1	4.1		4.2 4.1	4.2	
M3	Cloudy	Calm	10:00	Surface	1	23.3 23.2	23.3	8.5 8.5	8.5	33.5 33.6	33.6	89.7 88.0	88.9	6.3 6.2	6.3	6.3	1.8 2.2	2.0	3.1	4.9 4.9	4.9	5.5
				Middle	4	23.0 23.0	23.0	8.5 8.5	8.5	33.9 33.9	33.9	88.0 88.8	88.4	6.2 6.3	6.3		3.3 3.1	3.2		6.3 6.0	6.2	
				Bottom	7	23.0 23.0	23.0	8.5 8.5	8.5	34.0 34.0	34.0	89.9 89.9	89.9	6.3 6.4	6.4		4.1 4.1	4.1		5.5 5.5	5.5	
M4	Cloudy	Calm	09:29	Surface	1	23.2 23.1	23.2	8.5 8.5	8.5	33.6 33.7	33.7	89.2 89.7	89.5	6.3 6.3	6.3	6.4	1.9 2.3	2.1	2.5	4.8 4.8	4.8	4.6
				Middle	5	23.0 23.0	23.0	8.5 8.5	8.5	33.9 34.0	34.0	91.0 91.3	91.2	6.4 6.5	6.5		2.5 2.5	2.5		4.4 4.5	4.5	
				Bottom	9	22.9 23.0	23.0	8.5 8.6	8.6	34.0 34.0	34.0	92.3 92.0	92.2	6.5 6.5	6.5		2.9 2.7	2.8		4.5 4.3	4.4	
M5	Cloudy	Calm	10:14	Surface	1	23.2 23.2	23.2	8.4 8.5	8.5	33.5 33.5	33.5	89.8 90.5	90.2	6.3 6.4	6.4	6.4	1.5 1.4	1.5	2.5	4.9 4.8	4.9	4.2
				Middle	5.5	23.2 23.2	23.2	8.5 8.5	8.5	33.6 33.6	33.6	91.0 90.9	91.0	6.4 6.4	6.4		1.5 1.6	1.6		4.1 4.0	4.1	
				Bottom	10	23.0 23.0	23.0	8.5 8.5	8.5	33.9 33.9	33.9	89.8 89.8	89.8	6.3 6.3	6.3		4.2 4.4	4.3		3.6 3.5	3.6	
M6	Cloudy	Calm	10:10	Surface	-	-	-	-	-	-	-	-	-	-	-	6.2	-	-	3.0	-	-	6.8
				Middle	2	23.0 23.0	23.0	8.5 8.5	8.5	33.9 33.9	33.9	88.5 88.4	88.5	6.2 6.2	6.2		3.0 2.9	3.0		6.7 6.9	6.8	
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-	

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 25 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 5.2 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 6.0 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 5.9 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.4 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.9 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

**Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 25 April 2018**

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Cloudy	Calm	15:04	Surface	1	23.2 23.2	23.2	8.5 8.5	8.5	33.4 33.4	33.4	96.4 94.2	95.3	6.8 6.6	6.7	6.7	1.4 1.4	1.4	2.3	5.0 4.8	4.9	6.0
				Middle	10	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.7	33.7	95.7 95.0	95.4	6.7 6.7	6.7		1.3 1.3	1.3		7.9 7.6	7.8	
				Bottom	19	22.8 22.8	22.8	8.6 8.6	8.6	34.1 34.1	34.1	93.7 93.6	93.7	6.6 6.6	6.6		4.2 4.3	4.3		5.3 5.3	5.3	
C2	Cloudy	Calm	14:05	Surface	1	23.2 23.2	23.2	8.5 8.6	8.6	33.4 33.4	33.4	87.2 89.2	88.2	6.2 6.3	6.3	6.4	1.0 0.9	1.0	2.1	3.0 3.0	3.0	4.3
				Middle	17	23.0 23.0	23.0	8.6 8.6	8.6	33.9 33.9	33.9	91.7 91.7	91.7	6.5 6.5	6.5		1.6 1.6	1.6		6.6 6.6	6.6	
				Bottom	33	22.9 22.9	22.9	8.7 8.7	8.7	34.1 34.1	34.1	92.7 92.7	92.7	6.6 6.6	6.6		3.4 3.7	3.6		3.4 3.4	3.4	
G1	Cloudy	Calm	14:34	Surface	1	23.1 23.2	23.2	8.5 8.5	8.5	33.6 33.5	33.6	96.8 95.7	96.3	6.8 6.8	6.8	6.8	1.4 1.4	1.4	1.5	4.0 4.0	4.0	4.5
				Middle	4	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.6	33.7	94.5 95.8	95.2	6.7 6.8	6.8		1.5 1.4	1.5		4.2 4.0	4.1	
				Bottom	7	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.7	33.7	93.7 93.7	93.7	6.6 6.6	6.6		1.5 1.5	1.5		5.3 5.3	5.3	
G2	Cloudy	Calm	14:25	Surface	1	23.1 23.1	23.1	8.5 8.5	8.5	33.6 33.6	33.6	95.9 95.3	95.6	6.8 6.7	6.8	6.7	0.6 0.6	0.6	1.6	4.2 4.2	4.2	4.4
				Middle	5	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.7	33.7	93.0 93.1	93.1	6.6 6.6	6.6		2.4 2.7	2.6		3.7 3.7	3.7	
				Bottom	9	23.0 23.0	23.0	8.5 8.6	8.6	33.9 33.9	33.9	91.4 91.2	91.3	6.5 6.4	6.5		1.5 1.5	1.5		5.2 5.1	5.2	
G3	Cloudy	Calm	14:39	Surface	1	23.2 23.2	23.2	8.5 8.5	8.5	33.4 33.4	33.4	96.1 95.7	95.9	6.8 6.7	6.8	6.7	1.4 1.3	1.4	2.0	2.7 2.6	2.7	3.6
				Middle	4	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.7	33.7	92.7 92.7	92.7	6.5 6.5	6.5		1.5 1.7	1.6		2.9 3.0	3.0	
				Bottom	7	23.0 23.0	23.0	8.5 8.6	8.6	34.0 33.9	34.0	91.6 91.6	91.6	6.5 6.5	6.5		3.1 3.0	3.1		5.1 5.0	5.1	
G4	Cloudy	Calm	14:48	Surface	1	23.2 23.2	23.2	8.5 8.5	8.5	33.6 33.6	33.6	94.5 93.7	94.1	6.7 6.6	6.7	6.7	1.6 1.6	1.6	2.5	4.1 3.9	4.0	4.1
				Middle	4	23.2 23.2	23.2	8.5 8.5	8.5	33.7 33.7	33.7	93.2 94.1	93.7	6.6 6.6	6.6		1.7 1.6	1.7		4.6 4.7	4.7	
				Bottom	7	23.0 23.0	23.0	8.5 8.5	8.5	34.0 34.0	34.0	89.9 90.1	90.0	6.3 6.4	6.4		4.2 4.2	4.2		3.6 3.7	3.7	
M1	Cloudy	Calm	14:30	Surface	1	23.2 23.2	23.2	8.5 8.5	8.5	33.6 33.6	33.6	93.8 93.8	93.8	6.6 6.6	6.6	6.6	1.3 1.2	1.3	1.4	5.3 5.0	5.2	4.4
				Middle	3	23.2 23.1	23.2	8.5 8.5	8.5	33.6 33.7	33.7	93.3 92.8	93.1	6.6 6.5	6.6		1.3 1.4	1.4		3.9 3.8	3.9	
				Bottom	5	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.7	33.7	92.5 92.6	92.6	6.5 6.5	6.5		1.4 1.4	1.4		4.2 4.2	4.2	
M2	Cloudy	Calm	14:20	Surface	1	23.1 23.1	23.1	8.5 8.5	8.5	33.6 33.6	33.6	95.6 95.4	95.5	6.7 6.7	6.7	6.7	0.4 0.4	0.4	1.6	5.6 5.5	5.6	5.8
				Middle	6	23.1 23.1	23.1	8.5 8.5	8.5	33.7 33.7	33.7	94.1 93.9	94.0	6.6 6.6	6.6		0.6 0.6	0.6		6.8 5.6	6.2	
				Bottom	11	22.9 22.9	22.9	8.6 8.6	8.6	34.0 34.0	34.0	91.7 91.7	91.7	6.5 6.5	6.5		3.9 3.9	3.9		5.5 5.5	5.5	
M3	Cloudy	Calm	14:42	Surface	1	23.2 23.2	23.2	8.5 8.5	8.5	33.5 33.5	33.5	94.3 93.7	94.0	6.7 6.6	6.7	6.6	2.0 2.0	2.0	2.5	5.2 5.2	5.2	5.8
				Middle	4	23.1 23.1	23.1	8.5 8.5	8.5	33.8 33.8	33.8	92.2 91.8	92.0	6.5 6.5	6.5		2.6 2.6	2.6		8.9 8.9	8.9	
				Bottom	7	23.0 23.0	23.0	8.6 8.6	8.6	34.0 34.0	34.0	91.6 91.5	91.6	6.5 6.5	6.5		2.8 2.9	2.9		3.3 3.3	3.3	
M4	Cloudy	Calm	14:13	Surface	1	23.1 23.1	23.1	8.6 8.6	8.6	33.5 33.5	33.5	92.5 93.0	92.8	6.5 6.6	6.6	6.6	1.2 1.2	1.2	1.2	3.9 3.8	3.9	4.6
				Middle	5	23.1 23.1	23.1	8.6 8.6	8.6	33.7 33.7	33.7	93.0 93.2	93.1	6.6 6.6	6.6		1.1 1.2	1.2		4.3 4.2	4.3	
				Bottom	9	23.1 23.1	23.1	8.6 8.6	8.6	33.7 33.7	33.7	93.1 93.2	93.2	6.6 6.6	6.6		1.2 1.2	1.2		5.4 5.8	5.6	
M5	Cloudy	Calm	14:59	Surface	1	23.2 23.2	23.2	8.5 8.5	8.5	33.6 33.6	33.6	94.9 94.8	94.9	6.7 6.7	6.7	6.7	1.4 1.4	1.4	2.8	4.8 4.9	4.9	5.0
				Middle	5.5	23.1 23.1	23.1	8.5 8.5	8.5	33.8 33.8	33.8	93.3 93.0	93.2	6.6 6.6	6.6		2.0 2.1	2.1		5.0 5.0	5.0	
				Bottom	10	22.8 22.8	22.8	8.6 8.6	8.6	34.1 34.1	34.1	93.3 93.3	93.3	6.6 6.6	6.6		4.9 5.0	5.0		5.1 4.9	5.0	
M6	Cloudy	Calm	14:54	Surface	-	-	-	-	-	-	-	-	-	-	-	6.9	-	-	1.1	-	-	4.6
				Middle	2	23.2 23.2	23.2	8.5 8.5	8.5	33.7 33.7	33.7	97.4 97.4	97.4	6.9 6.9	6.9		1.1 1.1	1.1		4.6 4.5	4.6	
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-	

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 27 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.4 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.6 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.4 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.9 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.4 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.9 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 7.9 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 8.6 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 27 April 2018

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition*	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Fine	Calm	12:07	Surface	1	23.3 23.3	23.3	8.1 8.1	8.1	33.3 33.3	33.3	91.5 91.2	91.4	6.5 6.4	6.5	6.5	1.6 1.7	1.7	2.2	4.6 4.6	4.6	5.0
				Middle	10	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	91.1 90.8	91.0	6.4 6.4	6.4		1.6 1.8	1.7		5.6 5.3	5.5	
				Bottom	19	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	91.6 90.9	91.3	6.5 6.4	6.5		3.1 3.2	3.2		4.9 5.0	5.0	
C2	Fine	Calm	11:03	Surface	1	23.3 23.2	23.3	8.0 8.1	8.1	33.1 33.2	33.2	92.9 90.5	91.7	6.6 6.4	6.5	6.4	1.5 1.5	1.5	2.1	5.2 5.4	5.3	6.0
				Middle	16.5	23.2 23.2	23.2	8.0 8.1	8.1	33.2 33.2	33.2	89.5 89.5	89.5	6.3 6.3	6.3		2.1 1.9	2.0		6.2 6.2	6.2	
				Bottom	32	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	88.3 88.3	88.3	6.2 6.2	6.2		2.9 2.6	2.8		6.6 6.5	6.6	
G1	Fine	Calm	11:36	Surface	1	23.2 23.3	23.3	8.1 8.1	8.1	33.2 33.2	33.2	90.4 89.1	89.8	6.4 6.3	6.4	6.4	0.9 0.9	0.9	1.1	5.5 5.7	5.6	5.0
				Middle	4	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	91.3 90.6	91.0	6.4 6.4	6.4		1.1 1.2	1.2		5.4 5.5	5.5	
				Bottom	7	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	90.4 90.4	90.4	6.4 6.4	6.4		1.1 1.1	1.1		4.0 4.0	4.0	
G2	Fine	Calm	11:24	Surface	1	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	91.8 91.1	91.5	6.5 6.4	6.5	6.5	1.3 1.4	1.4	2.1	5.0 5.0	5.0	5.1
				Middle	5	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	90.8 90.7	90.8	6.4 6.4	6.4		1.7 1.8	1.8		5.7 5.5	5.6	
				Bottom	9	23.1 23.1	23.1	8.1 8.1	8.1	33.4 33.4	33.4	89.7 89.2	89.5	6.3 6.3	6.3		3.1 3.3	3.2		4.6 4.6	4.6	
G3	Fine	Calm	11:41	Surface	1	23.3 23.3	23.3	8.1 8.1	8.1	33.2 33.3	33.2	91.9 91.7	91.8	6.5 6.4	6.5	6.5	1.1 1.1	1.1	0.9	4.6 3.8	3.8	3.9
				Middle	4	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	91.2 90.7	91.0	6.4 6.4	6.4		0.9 0.8	0.9		4.2 4.1	4.2	
				Bottom	7	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	90.6 90.1	90.4	6.4 6.4	6.4		0.8 0.8	0.8		3.7 3.7	3.7	
G4	Fine	Calm	11:50	Surface	1	23.3 23.4	23.4	8.1 8.1	8.1	33.3 33.2	33.3	93.0 91.7	92.4	6.6 6.5	6.6	6.6	0.9 1.1	1.0	1.5	3.0 3.0	3.0	4.9
				Middle	4	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	91.7 91.6	91.7	6.5 6.5	6.5		0.9 1.0	1.0		5.2 5.2	5.2	
				Bottom	7	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	85.9 87.2	86.6	6.1 6.2	6.2		2.3 2.5	2.4		6.3 6.4	6.4	
M1	Fine	Calm	11:30	Surface	1	23.3 23.3	23.3	8.1 8.1	8.1	33.2 33.2	33.2	88.3 87.0	87.7	6.2 6.1	6.2	6.3	1.5 1.6	1.6	1.6	5.5 5.5	5.5	5.3
				Middle	3	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	90.3 90.0	90.2	6.4 6.4	6.4		1.3 1.4	1.4		5.1 5.1	5.1	
				Bottom	5	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	90.2 89.9	90.1	6.4 6.3	6.4		1.9 1.7	1.8		5.3 5.0	5.2	
M2	Fine	Calm	11:18	Surface	1	23.3 23.3	23.3	8.1 8.1	8.1	33.3 33.2	33.3	92.9 92.4	92.7	6.5 6.5	6.5	6.6	1.0 0.9	1.0	1.4	4.1 4.2	4.2	5.8
				Middle	5.5	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	93.2 93.2	93.2	6.6 6.6	6.6		1.2 1.2	1.2		6.6 6.7	6.7	
				Bottom	10	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	92.1 90.9	91.5	6.5 6.4	6.5		1.9 2.0	2.0		6.5 6.3	6.4	
M3	Fine	Calm	11:45	Surface	1	23.3 23.5	23.4	8.1 8.1	8.1	33.2 33.2	33.2	90.7 90.7	90.7	6.4 6.5	6.5	6.5	1.0 1.0	1.0	1.1	5.3 5.3	5.3	5.6
				Middle	4	23.2 23.3	23.3	8.1 8.1	8.1	33.3 33.3	33.3	91.4 91.2	91.3	6.5 6.5	6.5		0.7 0.7	0.7		5.7 5.7	5.7	
				Bottom	7	23.2 23.3	23.3	8.1 8.1	8.1	33.4 33.3	33.4	89.3 90.2	89.8	6.2 6.1	6.2		1.7 1.7	1.7		5.7 5.8	5.8	
M4	Fine	Calm	11:11	Surface	1	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.4	33.4	90.9 91.2	91.1	6.4 6.4	6.4	6.5	1.7 1.7	1.7	2.3	4.4 4.2	4.3	5.6
				Middle	5	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	91.4 90.7	91.1	6.5 6.4	6.5		2.3 2.6	2.5		7.0 6.9	7.0	
				Bottom	9	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	90.4 90.5	90.5	6.4 6.4	6.4		2.8 2.7	2.8		5.4 5.5	5.5	
M5	Fine	Calm	12:01	Surface	1	23.3 23.2	23.3	8.1 8.1	8.1	33.3 33.4	33.4	90.8 90.2	90.5	6.4 6.4	6.4	6.4	2.4 2.8	2.6	2.4	5.6 5.4	5.5	4.7
				Middle	5.5	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	90.8 90.4	90.6	6.4 6.4	6.4		1.9 1.9	1.9		4.4 4.3	4.4	
				Bottom	10	23.2 23.2	23.2	8.1 8.1	8.1	33.5 33.5	33.5	91.9 91.5	91.7	6.5 6.5	6.5		2.9 2.7	2.8		4.2 4.2	4.2	
M6	Fine	Calm	11:56	Surface	-	-	-	-	-	-	-	-	-	-	6.5	-	-	1.1	-	-	7.1	
				Middle	2	23.2 23.2	23.2	8.1 8.1	8.1	33.2 33.2	33.2	91.7 91.7	91.7	6.5 6.5		6.5	1.1 1.1		1.1	7.0 7.1		7.1
				Bottom	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 27 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 8.0 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 8.7 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.2 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.8 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 6.2 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 6.8 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.3 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.9 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 27 April 2018

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition*	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity (NTU)			Suspended Solids (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*
C1	Fine	Calm	16:26	Surface	1	23.3 23.3	23.3	8.1 8.1	8.1	33.3 33.3	33.3	93.0 92.4	92.7	6.6 6.5	6.6	6.6	1.3 1.4	1.4	3.3	5.1 5.2	5.2	5.6
				Middle	10	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	92.4 92.5	92.5	6.5 6.5	6.5		1.9 1.8	1.9		5.5 5.4	5.5	
				Bottom	19	23.2 23.2	23.2	8.1 8.1	8.1	33.5 33.5	33.5	91.7 91.3	91.5	6.5 6.4	6.5		6.8 6.6	6.7		6.0 6.2	6.1	
C2	Fine	Calm	15:30	Surface	1	23.5 23.4	23.5	8.0 8.0	8.0	33.3 33.1	33.1	91.9 90.3	91.1	6.5 6.4	6.5	6.5	1.3 1.3	1.3	2.2	5.1 5.0	5.1	5.9
				Middle	16.5	23.2 23.2	23.2	8.0 8.0	8.0	33.3 33.3	33.3	90.1 89.9	90.0	6.4 6.3	6.4		2.2 2.5	2.4		7.3 7.2	7.3	
				Bottom	32	23.2 23.2	23.2	8.0 8.0	8.0	33.3 33.3	33.3	89.8 90.3	90.1	6.3 6.4	6.4		2.9 2.9	2.9		5.2 5.2	5.2	
G1	Fine	Calm	15:57	Surface	1	23.7 24.0	23.9	8.1 8.1	8.1	33.2 33.2	33.2	97.3 97.4	97.4	6.8 6.8	6.8	6.8	0.9 0.9	0.9	1.1	5.6 5.5	5.6	5.9
				Middle	4	23.7 23.8	23.8	8.1 8.1	8.1	33.2 33.2	33.2	96.8 96.6	96.7	6.8 6.8	6.8		0.9 0.9	0.9		7.4 7.4	7.3	
				Bottom	7	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.4	33.4	92.9 91.6	92.3	6.6 6.5	6.6		1.7 1.5	1.6		4.6 4.7	4.7	
G2	Fine	Calm	15:47	Surface	1	23.7 23.7	23.7	8.1 8.1	8.1	33.2 33.3	33.3	96.1 96.5	96.3	6.7 6.8	6.8	6.8	0.9 1.0	1.0	0.9	5.8 5.9	5.9	8.3
				Middle	5	23.3 23.4	23.4	8.1 8.1	8.1	33.3 33.3	33.3	96.0 96.4	96.2	6.8 6.8	6.8		0.7 0.7	0.7		13.0 12.9	13.0	
				Bottom	9	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.3	33.4	93.2 94.8	94.0	6.6 6.7	6.7		1.1 1.0	1.1		6.1 6.0	6.1	
G3	Fine	Calm	16:02	Surface	1	24.1 23.8	24.0	8.1 8.1	8.1	33.1 33.1	33.1	96.7 95.3	96.0	6.7 6.7	6.7	6.7	1.2 1.4	1.3	1.0	4.4 4.4	4.4	3.8
				Middle	4	23.3 23.3	23.3	8.1 8.1	8.1	33.3 33.3	33.3	95.7 94.9	95.3	6.7 6.7	6.7		0.9 1.0	1.0		3.8 3.9	3.9	
				Bottom	7	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	92.7 93.1	92.9	6.5 6.6	6.6		0.8 0.8	0.8		3.2 3.1	3.2	
G4	Fine	Calm	16:12	Surface	1	23.6 23.9	23.9	8.1 8.1	8.1	33.2 33.2	33.2	96.9 97.3	97.1	6.8 6.8	6.8	6.8	0.9 0.6	0.9	1.0	4.8 4.9	4.9	5.2
				Middle	4	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	94.6 95.2	94.9	6.7 6.7	6.7		0.6 0.9	0.9		5.0 5.2	5.1	
				Bottom	7	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	91.5 94.0	92.9	6.5 6.6	6.6		1.3 1.3	1.3		5.7 5.7	5.7	
M1	Fine	Calm	15:52	Surface	1	23.6 23.9	23.9	8.1 8.1	8.1	33.2 33.2	33.2	97.0 96.9	97.0	6.8 6.8	6.8	6.8	0.9 0.8	0.9	1.1	5.7 5.8	5.8	5.6
				Middle	3	23.7 23.8	23.8	8.1 8.1	8.1	33.2 33.2	33.2	96.2 96.4	96.3	6.7 6.7	6.7		1.0 1.0	1.0		6.0 6.0	5.9	
				Bottom	5	23.5 23.5	23.5	8.1 8.1	8.1	33.3 33.3	33.3	94.2 94.2	94.2	6.6 6.6	6.6		1.3 1.2	1.3		5.1 5.1	5.1	
M2	Fine	Calm	15:43	Surface	1	23.5 23.5	23.5	8.1 8.1	8.1	33.3 33.3	33.3	96.7 96.0	96.4	6.8 6.7	6.8	6.8	1.0 1.0	1.0	1.5	2.5 2.6	2.6	3.9
				Middle	6	23.2 23.3	23.3	8.1 8.1	8.1	33.4 33.3	33.4	94.4 93.6	94.0	6.7 6.6	6.7		1.2 1.2	1.2		5.6 5.6	5.6	
				Bottom	11	23.2 23.2	23.2	8.1 8.1	8.1	33.4 33.4	33.4	92.4 92.0	92.2	6.5 6.5	6.5		2.4 2.3	2.4		3.5 3.5	3.5	
M3	Fine	Calm	16:06	Surface	1	24.2 23.7	24.0	8.1 8.1	8.1	32.9 33.1	33.0	95.8 95.4	95.6	6.7 6.7	6.7	6.7	1.3 1.3	1.3	1.1	5.4 5.4	5.4	4.7
				Middle	4	23.3 23.3	23.3	8.1 8.1	8.1	33.3 33.3	33.3	95.1 95.5	95.3	6.7 6.7	6.7		0.9 1.0	1.0		5.4 5.6	5.5	
				Bottom	7	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	93.1 93.3	93.2	6.6 6.6	6.6		1.0 0.9	1.0		3.2 3.1	3.2	
M4	Fine	Calm	15:37	Surface	1	23.5 23.5	23.5	8.1 8.1	8.1	33.3 33.3	33.3	94.6 96.1	95.4	6.7 6.8	6.8	6.8	1.2 1.1	1.2	1.1	5.2 5.3	5.3	4.6
				Middle	5	23.3 23.3	23.3	8.1 8.1	8.1	33.4 33.4	33.4	96.2 96.1	96.2	6.8 6.8	6.8		1.1 1.0	1.1		4.6 4.6	4.6	
				Bottom	9	23.3 23.3	23.3	8.1 8.1	8.1	33.4 33.4	33.4	96.2 95.9	96.1	6.8 6.8	6.8		1.0 1.1	1.1		3.9 3.9	3.9	
M5	Fine	Calm	16:21	Surface	1	23.4 23.4	23.4	8.1 8.1	8.1	33.2 33.2	33.2	92.3 91.3	91.8	6.5 6.4	6.5	6.5	1.4 1.4	1.4	1.9	5.3 5.3	5.3	5.2
				Middle	6	23.3 23.3	23.3	8.1 8.1	8.1	33.3 33.3	33.3	90.8 90.7	90.8	6.4 6.4	6.4		1.6 1.9	1.8		4.5 4.7	4.6	
				Bottom	11	23.3 23.3	23.3	8.1 8.1	8.1	33.3 33.3	33.3	90.0 89.8	89.9	6.3 6.3	6.3		2.2 2.5	2.4		5.6 5.5	5.6	
M6	Fine	Calm	16:17	Surface	-	-	-	-	-	-	-	-	-	-	6.3	-	-	2.5	-	-	4.5	
				Middle	2	23.2 23.2	23.2	8.1 8.1	8.1	33.3 33.3	33.3	89.7 89.7	89.7	6.3 6.3		6.3	2.4 2.5		2.5	4.5 4.4		4.5
				Bottom	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 30 April 2018 (Mid-Ebb Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.1 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>C2: 3.4 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.4 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.9 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.4 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.9 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>C2: 6.1 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>C2: 6.6 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.

Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 30 April 2018

(Mid-Ebb Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)	Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
C1	Cloudy	Moderate	12:38	Surface	1	23.9 23.9	23.9	8.1 8.1	8.1	33.1 33.1	33.1	91.3 91.6	91.5	6.4 6.4	6.4	6.5	1.5 1.7	1.6	1.8	4.9 4.7	4.8	4.8
				Middle	10	23.7 23.7	23.7	8.1 8.1	8.1	33.3 33.3	33.3	92.4 92.0	92.2	6.5 6.4	6.5		1.9 1.8	1.9		5.4 5.5	5.5	
				Bottom	19	23.7 23.7	23.7	8.1 8.1	8.1	33.4 33.4	33.4	92.9 93.0	93.0	6.5 6.5	6.5		1.8 2.1	2.0		4.1 4.1	4.1	
C2	Cloudy	Moderate	11:29	Surface	1	23.8 23.8	23.8	8.0 8.0	8.0	33.1 33.1	33.1	91.5 90.0	90.8	6.4 6.3	6.4	6.4	2.0 1.9	2.0	2.1	5.3 5.3	5.3	5.3
				Middle	16.5	23.7 23.7	23.7	8.0 8.0	8.0	33.1 33.2	33.2	90.1 89.8	90.0	6.3 6.3	6.3		1.6 1.9	1.8		5.6 5.6	5.6	
				Bottom	32	23.7 23.6	23.7	8.0 8.1	8.1	33.2 33.3	33.3	89.6 89.7	89.6	6.3 6.3	6.3		2.5 2.7	2.6		5.1 5.1	5.1	
G1	Cloudy	Moderate	12:04	Surface	1	23.9 23.8	23.9	8.1 8.1	8.1	33.2 33.2	33.2	93.8 93.6	93.7	6.6 6.5	6.6	6.6	1.0 1.0	1.0	1.7	5.1 5.2	5.2	5.2
				Middle	4	23.7 23.7	23.7	8.1 8.1	8.1	33.3 33.3	33.3	93.7 93.4	93.6	6.6 6.5	6.6		1.8 1.5	1.7		5.9 5.8	5.9	
				Bottom	7	23.7 23.6	23.7	8.1 8.1	8.1	33.4 33.4	33.4	93.8 93.5	93.7	6.6 6.6	6.6		2.3 2.4	2.4		4.4 4.4	4.4	
G2	Cloudy	Moderate	11:53	Surface	1	23.8 23.9	23.9	8.1 8.1	8.1	33.2 33.2	33.2	95.6 95.5	95.6	6.7 6.7	6.7	6.7	1.4 1.2	1.3	1.3	4.3 4.2	4.3	4.9
				Middle	5	23.7 23.7	23.7	8.1 8.1	8.1	33.4 33.4	33.4	95.2 95.2	95.2	6.7 6.7	6.7		1.3 1.1	1.2		5.2 5.0	5.1	
				Bottom	9	23.6 23.6	23.6	8.1 8.1	8.1	33.4 33.4	33.4	94.6 94.9	94.8	6.6 6.6	6.6		1.5 1.3	1.4		5.4 5.3	5.4	
G3	Cloudy	Moderate	12:10	Surface	1	23.9 23.8	23.9	8.1 8.1	8.1	33.1 33.1	33.1	93.3 92.4	92.9	6.5 6.5	6.5	6.5	1.0 1.1	1.1	1.4	5.8 5.8	5.8	4.0
				Middle	4	23.7 23.7	23.7	8.1 8.1	8.1	33.2 33.2	33.2	91.5 91.4	91.5	6.4 6.4	6.4		1.6 1.6	1.6		3.6 3.7	3.7	
				Bottom	7	23.6 23.6	23.6	8.1 8.1	8.1	33.3 33.3	33.3	92.3 91.2	91.8	6.5 6.4	6.5		1.3 1.6	1.5		2.6 2.5	2.6	
G4	Cloudy	Moderate	12:20	Surface	1	23.8 23.8	23.8	8.1 8.1	8.1	33.2 33.2	33.2	94.5 93.9	94.1	6.6 6.6	6.6	6.5	0.9 0.9	0.9	1.8	2.7 2.7	2.8	3.4
				Middle	4	23.6 23.6	23.6	8.1 8.1	8.1	33.3 33.3	33.3	91.2 90.5	90.9	6.4 6.3	6.4		2.0 2.2	2.1		4.4 4.4	4.4	
				Bottom	7	23.6 23.6	23.6	8.1 8.1	8.1	33.4 33.4	33.4	92.4 91.4	91.9	6.5 6.4	6.5		2.4 2.1	2.3		2.8 2.9	2.9	
M1	Cloudy	Moderate	11:59	Surface	1	23.9 23.8	23.9	8.1 8.1	8.1	33.2 33.2	33.2	94.0 93.8	93.9	6.6 6.6	6.6	6.6	1.5 1.6	1.6	1.8	3.6 3.5	3.6	4.9
				Middle	3	23.7 23.8	23.8	8.1 8.1	8.1	33.3 33.3	33.3	94.0 93.6	93.8	6.6 6.5	6.6		1.8 1.7	1.8		5.6 5.6	5.6	
				Bottom	5	23.7 23.7	23.7	8.1 8.1	8.1	33.3 33.3	33.3	94.2 93.9	94.1	6.6 6.6	6.6		2.2 2.0	2.1		5.3 5.4	5.4	
M2	Cloudy	Moderate	11:48	Surface	1	23.9 23.9	23.9	8.1 8.1	8.1	33.2 33.2	33.2	95.9 95.8	95.9	6.7 6.7	6.7	6.7	0.7 0.8	0.8	1.2	4.6 4.7	4.7	5.1
				Middle	5.5	23.7 23.7	23.7	8.1 8.1	8.1	33.3 33.3	33.3	95.7 95.3	95.5	6.7 6.7	6.7		0.9 0.9	0.9		7.3 7.5	7.4	
				Bottom	10	23.6 23.6	23.6	8.1 8.1	8.1	33.4 33.4	33.4	93.6 94.1	93.9	6.6 6.6	6.6		1.9 1.6	1.8		3.3 3.3	3.3	
M3	Cloudy	Moderate	12:15	Surface	1	23.8 23.8	23.8	8.1 8.1	8.1	33.1 33.1	33.1	90.1 92.0	91.1	6.3 6.4	6.4	6.4	1.0 1.1	1.1	1.4	4.3 4.3	4.3	4.4
				Middle	4	23.7 23.7	23.7	8.1 8.1	8.1	33.2 33.2	33.2	91.5 92.0	91.8	6.4 6.4	6.4		0.9 0.9	0.9		4.1 4.1	4.1	
				Bottom	7	23.6 23.6	23.6	8.1 8.1	8.1	33.3 33.3	33.3	89.1 89.5	89.3	6.2 6.3	6.3		2.4 2.2	2.3		4.6 4.7	4.7	
M4	Cloudy	Moderate	11:38	Surface	1	23.7 23.7	23.7	8.1 8.1	8.1	33.3 33.3	33.3	91.6 91.3	91.5	6.4 6.4	6.4	6.4	2.2 2.1	2.2	2.3	5.7 6.0	5.9	5.1
				Middle	5	23.6 23.6	23.6	8.1 8.1	8.1	33.3 33.3	33.3	91.4 91.2	91.3	6.4 6.4	6.4		2.2 2.2	2.2		3.6 3.8	3.7	
				Bottom	9	23.6 23.6	23.6	8.1 8.1	8.1	33.4 33.4	33.4	90.4 91.4	90.9	6.3 6.4	6.4		2.6 2.5	2.6		5.5 5.8	5.7	
M5	Cloudy	Moderate	12:31	Surface	1	23.8 23.8	23.8	8.1 8.1	8.1	33.2 33.2	33.2	93.4 93.9	93.7	6.5 6.6	6.6	6.6	1.3 1.4	1.4	1.5	4.2 4.2	4.2	3.6
				Middle	5.5	23.7 23.7	23.7	8.1 8.1	8.1	33.3 33.3	33.3	94.6 94.2	94.4	6.6 6.6	6.6		1.2 1.3	1.3		3.3 3.3	3.3	
				Bottom	10	23.6 23.6	23.6	8.1 8.1	8.1	33.4 33.4	33.4	94.0 94.1	94.1	6.6 6.6	6.6		1.7 1.7	1.7		3.3 3.1	3.2	
M6	Cloudy	Moderate	12:25	Surface	-	-	-	-	-	-	-	-	-	-	-	6.5	-	-	1.0	-	-	4.2
				Middle	1.5	23.7 23.7	23.7	8.1 8.1	8.1	33.2 33.2	33.2	92.4 92.5	92.5	6.5 6.5	6.5		1.0 1.0	1.0		4.1 4.3	4.2	
				Bottom	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-	

Remarks: *DA: Depth-Averaged
 **Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Appendix I - Action and Limit Levels for Marine Water Quality on 30 April 2018 (Mid-Flood Tide)

Parameter (unit)	Depth	Action Level	Limit Level
DO in mg/L (See Note 1 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Depth Average	<u>4.9 mg/L</u>	<u>4.6 mg/L</u>
	Bottom	<u>4.2 mg/L</u>	<u>3.6 mg/L</u>
	<u>Station M6</u>		
	Intake Level	<u>5.0 mg/L</u>	<u>4.7 mg/L</u>
Turbidity in NTU (See Note 2 and 4)	<u>Stations G1-G4, M1-M5</u>		
	Bottom	<u>19.3 NTU</u> or 120% of upstream control station's Turbidity at the same tide of the same day <u>CI: 2.6 NTU</u>	<u>22.2 NTU</u> or 130% of upstream control station's Turbidity at the same tide of the same day <u>CI: 2.9 NTU</u>
	<u>Station M6</u>		
	Intake Level	<u>19.0 NTU</u>	<u>19.4 NTU</u>
	SS in mg/L (See Note 2 and 4)	<u>Stations G1-G4</u>	
Surface		<u>6.0 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.1 mg/L</u>	<u>6.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.7 mg/L</u>
<u>Stations M1-M5</u>			
Surface		<u>6.2 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.1 mg/L</u>	<u>7.4 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.7 mg/L</u>
<u>Stations G1-G4, M1-M5</u>			
Bottom		<u>6.9 mg/L</u> or 120% of upstream control station's SS at the same tide of the same day <u>CI: 7.1 mg/L</u>	<u>7.9 mg/L</u> or 130% of upstream control station's SS at the same tide of the same day <u>CI: 7.7 mg/L</u>
<u>Station M6</u>			
Intake Level	<u>8.3 mg/L</u>	<u>8.6 mg/L</u>	

Notes:

1. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
2. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
3. All the figures given in the table are used for reference only and EPD may amend the figures whenever it is considered as necessary.
4. Action and limit values are derived based on baseline water quality monitoring results to show the actual baseline water quality condition.


Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Water Quality Monitoring Results on 30 April 2018

(Mid-Flood Tide)

Location	Weather Condition	Sea Condition**	Sampling Time	Depth (m)	Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)			
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
C1	Cloudy	Moderate	18:47	Surface	1	24.1 24.1	24.1	8.0 8.0	8.0	32.7 32.7	32.7	86.5 86.9	86.7	6.0 6.1	6.1	6.2	1.5 1.7	1.6	1.8	5.8 5.9	5.9	4.8
				Middle	10	23.8 23.8	23.8	8.1 8.1	8.1	33.2 33.2	33.2	89.9 89.5	89.7	6.3 6.3	6.3	6.3	1.6 1.5	1.6		2.6 2.6	2.6	
				Bottom	19	23.6 23.7	23.7	8.1 8.1	8.1	33.5 33.3	33.4	93.4 91.8	92.6	6.5 6.4	6.5	6.5	2.2 2.2	2.2		5.9 5.9	5.9	
C2	Cloudy	Moderate	17:38	Surface	1	24.2 24.2	24.2	8.0 8.0	8.0	32.5 32.5	32.5	85.1 85.1	85.1	5.9 5.9	5.9	6.2	1.6 1.6	1.6	2.0	4.7 4.6	4.7	5.8
				Middle	16	23.8 23.8	23.8	8.1 8.1	8.1	33.2 33.2	33.2	92.4 92.0	92.2	6.5 6.4	6.5	6.5	2.0 2.1	2.1		6.9 7.1	7.0	
				Bottom	31	23.7 23.7	23.7	8.1 8.1	8.1	33.3 33.3	33.3	92.7 92.5	92.6	6.5 6.5	6.5	6.5	2.3 2.3	2.3		5.6 5.7	5.7	
G1	Cloudy	Moderate	18:12	Surface	1	24.3 24.4	24.4	8.1 8.1	8.1	33.1 33.1	33.1	99.7 99.6	99.7	6.9 6.9	6.9	6.9	0.8 0.8	0.8	1.2	5.5 5.6	5.6	5.6
				Middle	4	24.0 23.9	24.0	8.1 8.1	8.1	33.2 33.2	33.2	98.3 98.1	98.2	6.9 6.8	6.9	6.9	0.9 0.9	0.9		6.8 6.6	6.7	
				Bottom	7	23.6 23.6	23.6	8.1 8.1	8.1	33.4 33.5	33.5	95.1 95.8	95.5	6.7 6.7	6.7	6.7	1.9 2.1	2.0		4.4 4.4	4.4	
G2	Cloudy	Moderate	18:02	Surface	1	24.4 24.4	24.4	8.1 8.1	8.1	33.1 33.1	33.1	99.6 99.2	99.4	6.9 6.9	6.9	6.9	0.8 0.9	0.9	1.5	5.0 5.1	5.1	4.0
				Middle	5	23.8 23.7	23.8	8.1 8.1	8.1	33.3 33.3	33.3	97.2 97.0	97.1	6.8 6.8	6.8	6.8	1.1 1.0	1.1		2.7 2.8	2.8	
				Bottom	9	23.6 23.6	23.6	8.1 8.1	8.1	33.5 33.5	33.5	94.2 94.9	94.6	6.6 6.6	6.6	6.6	2.3 2.5	2.4		3.9 4.0	4.0	
G3	Cloudy	Moderate	18:17	Surface	1	24.6 24.6	24.6	8.1 8.1	8.1	33.1 33.1	33.1	99.7 99.2	99.5	6.9 6.8	6.9	6.7	0.7 0.8	0.8	1.6	5.6 5.7	5.7	5.6
				Middle	4	23.9 23.8	23.9	8.1 8.1	8.1	33.2 33.2	33.2	93.6 93.1	93.4	6.5 6.5	6.5	6.5	2.0 1.9	2.0		5.6 5.7	5.7	
				Bottom	7	23.6 23.7	23.7	8.1 8.1	8.1	33.4 33.4	33.4	94.4 94.1	94.3	6.6 6.6	6.6	6.6	2.2 2.0	2.1		5.3 5.4	5.4	
G4	Cloudy	Moderate	18:29	Surface	1	24.3 24.2	24.3	8.1 8.1	8.1	33.1 33.2	33.2	98.6 99.1	98.9	6.8 6.9	6.9	6.9	1.5 1.5	1.5	1.7	5.0 5.1	5.1	4.2
				Middle	4	24.0 24.0	24.0	8.1 8.1	8.1	33.2 33.2	33.2	98.5 98.0	98.3	6.9 6.8	6.9	6.9	1.3 1.6	1.5		4.5 4.6	4.6	
				Bottom	7	23.7 23.7	23.7	8.1 8.1	8.1	33.4 33.3	33.4	96.4 96.5	96.5	6.7 6.7	6.7	6.7	2.1 2.0	2.1		3.0 3.0	3.0	
M1	Cloudy	Moderate	18:08	Surface	1	24.4 24.4	24.4	8.1 8.1	8.1	33.1 33.1	33.1	93.9 93.2	93.6	6.5 6.5	6.5	6.5	1.3 1.4	1.4	1.3	2.6 2.7	2.7	3.1
				Middle	3	24.2 24.2	24.2	8.1 8.1	8.1	33.1 33.1	33.1	92.0 91.1	91.6	6.4 6.3	6.4	6.4	1.4 1.4	1.4		3.3 3.2	3.3	
				Bottom	5	23.8 23.8	23.8	8.1 8.1	8.1	33.2 33.2	33.2	93.0 93.6	93.3	6.5 6.5	6.5	6.5	1.2 1.2	1.2		3.2 3.2	3.2	
M2	Cloudy	Moderate	17:55	Surface	1	24.2 24.4	24.3	8.1 8.1	8.1	33.2 33.2	33.2	100.0 100.0	100.0	6.9 6.9	6.9	6.9	0.8 0.9	0.9	1.4	2.7 2.7	2.7	3.1
				Middle	5.5	24.2 24.2	24.2	8.1 8.1	8.1	33.2 33.2	33.2	99.2 99.3	99.3	6.9 6.9	6.9	6.9	0.9 0.9	0.9		4.4 4.4	4.4	
				Bottom	10	23.6 23.6	23.6	8.1 8.1	8.1	33.4 33.5	33.5	94.3 93.9	94.1	6.6 6.6	6.6	6.6	2.3 2.5	2.4		2.1 2.0	2.1	
M3	Cloudy	Moderate	18:22	Surface	1	24.6 24.6	24.6	8.1 8.1	8.1	33.1 33.0	33.1	98.4 98.4	98.4	6.8 6.8	6.8	6.8	0.8 0.8	0.8	1.7	3.0 2.9	3.0	3.9
				Middle	4	23.9 23.9	23.9	8.1 8.1	8.1	33.2 33.2	33.2	95.7 96.6	96.2	6.7 6.7	6.7	6.7	1.6 1.7	1.7		2.8 2.9	2.9	
				Bottom	7	23.6 23.6	23.6	8.1 8.1	8.1	33.5 33.4	33.5	93.4 90.3	91.9	6.5 6.3	6.4	6.4	2.5 2.5	2.5		5.8 6.0	5.9	
M4	Cloudy	Moderate	17:48	Surface	1	24.2 24.2	24.2	8.1 8.1	8.1	33.2 33.2	33.2	96.7 99.6	98.2	6.7 6.9	6.8	6.9	1.0 0.9	1.0	1.1	5.3 5.3	5.3	4.4
				Middle	5	24.1 24.2	24.2	8.1 8.1	8.1	33.2 33.2	33.2	99.4 100.1	99.8	6.9 7.0	7.0	6.9	1.0 0.9	1.0		3.4 3.4	3.4	
				Bottom	9	23.8 23.8	23.8	8.1 8.1	8.1	33.3 33.3	33.3	98.5 97.7	98.1	6.9 6.8	6.9	6.9	1.1 1.2	1.2		4.5 4.4	4.5	
M5	Cloudy	Moderate	18:40	Surface	1	24.1 24.1	24.1	8.0 8.0	8.0	32.8 32.8	32.8	89.3 88.8	89.1	6.2 6.2	6.2	6.2	1.5 1.5	1.5	1.7	5.4 5.6	5.5	6.1
				Middle	5.5	24.0 24.0	24.0	8.0 8.0	8.0	32.9 32.9	32.9	88.6 88.4	88.5	6.2 6.2	6.2	6.2	1.7 1.7	1.6		6.5 6.7	6.6	
				Bottom	10	24.0 24.0	24.0	8.1 8.1	8.1	32.9 33.0	33.0	88.3 88.2	88.3	6.2 6.2	6.2	6.2	1.9 2.1	2.0		6.0 6.1	6.1	
M6	Cloudy	Moderate	18:35	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	1.1	-	-	3.8
				Middle	1.5	24.3 24.3	24.3	8.1 8.1	8.1	33.2 33.2	33.2	98.5 98.7	98.6	6.8 6.8	6.8	6.8	1.1 1.1	1.1		3.9 3.7	3.8	
				Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-	-	

Remarks: *DA: Depth-Averaged
**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Dissolved Oxygen (Depth-averaged) at Mid-Ebb Tide

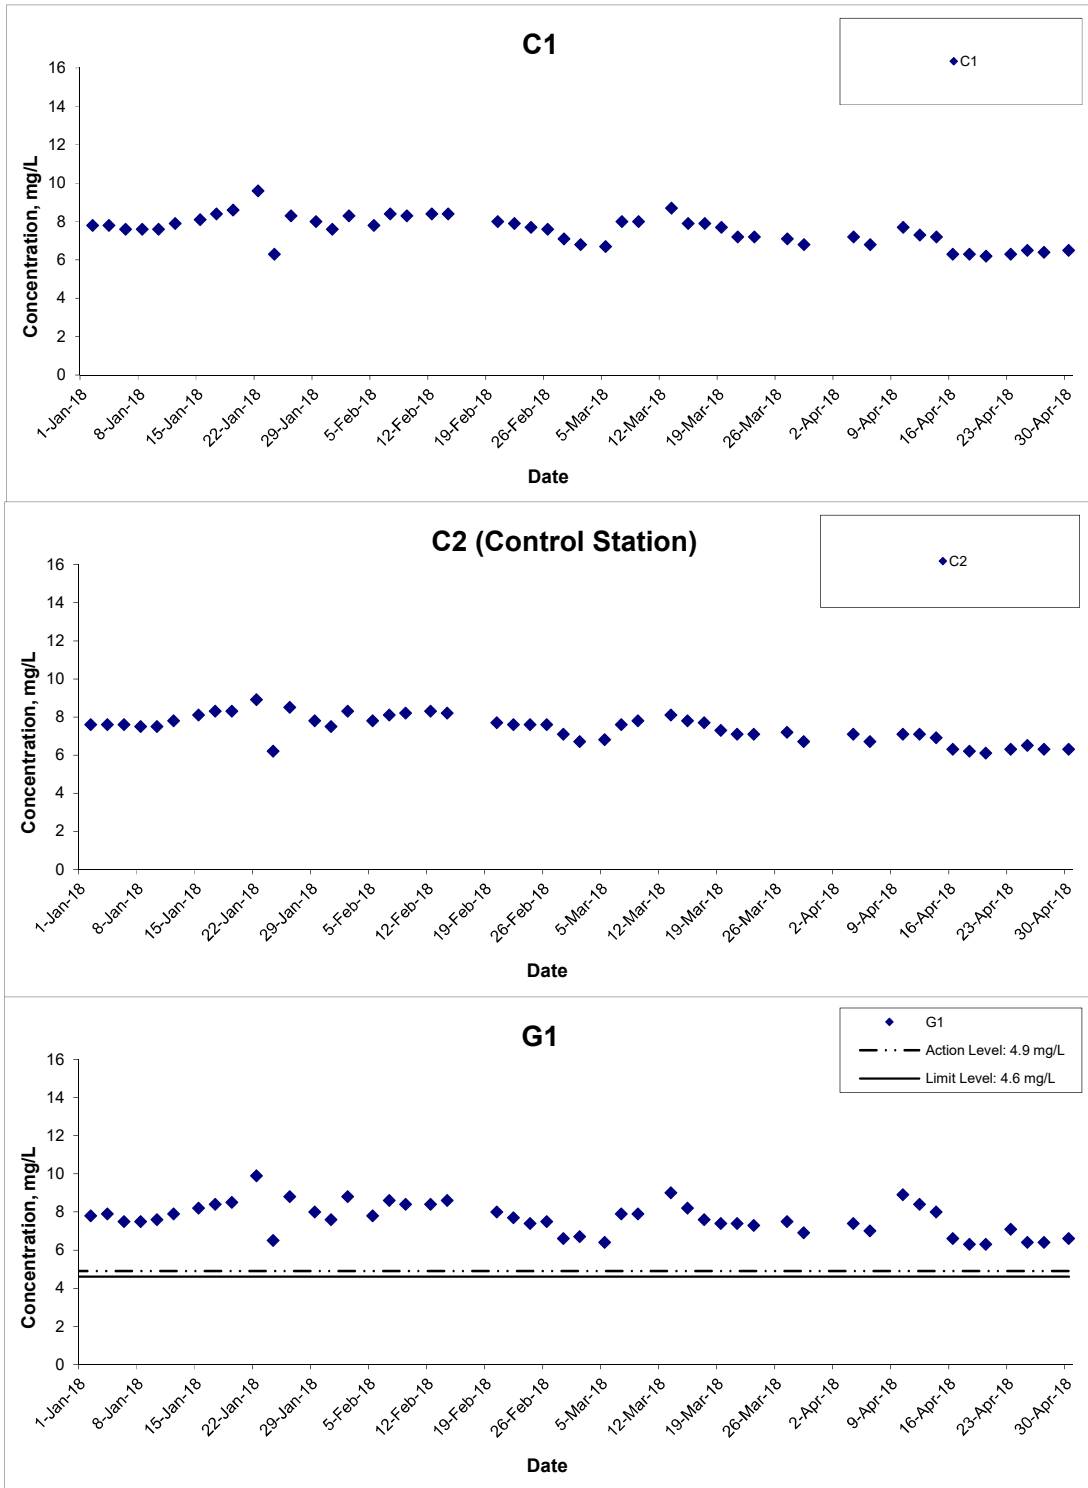

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Depth-averaged) at Mid-Ebb Tide

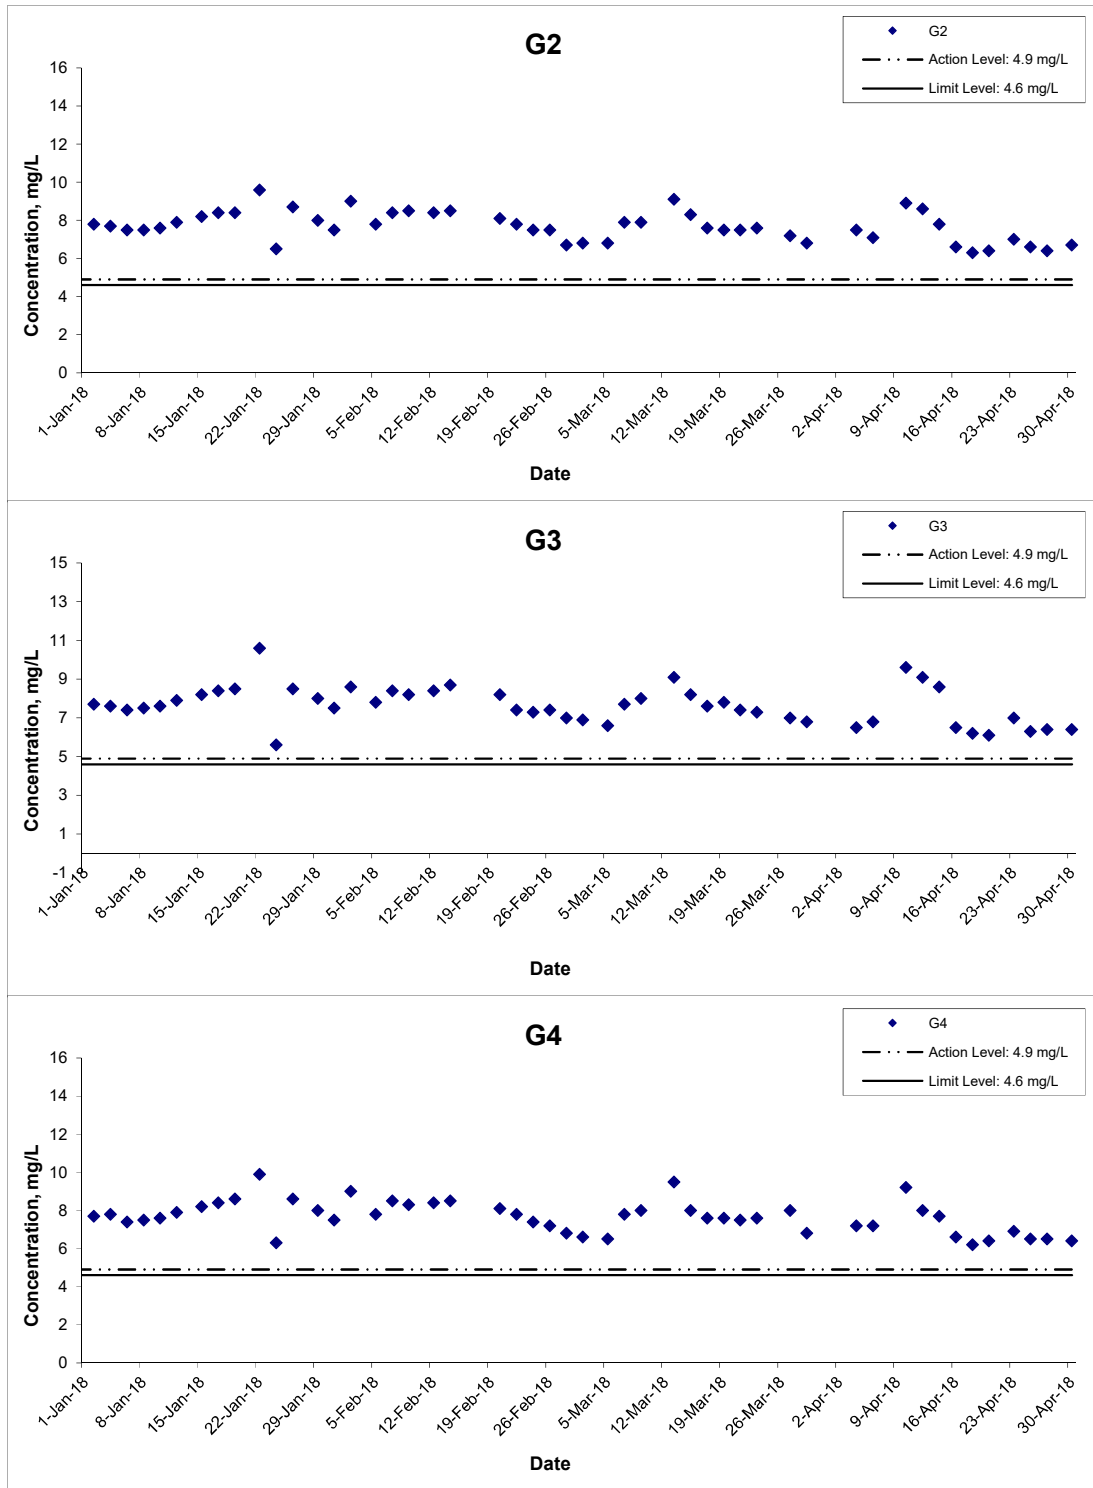

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Depth-averaged) at Mid-Ebb Tide

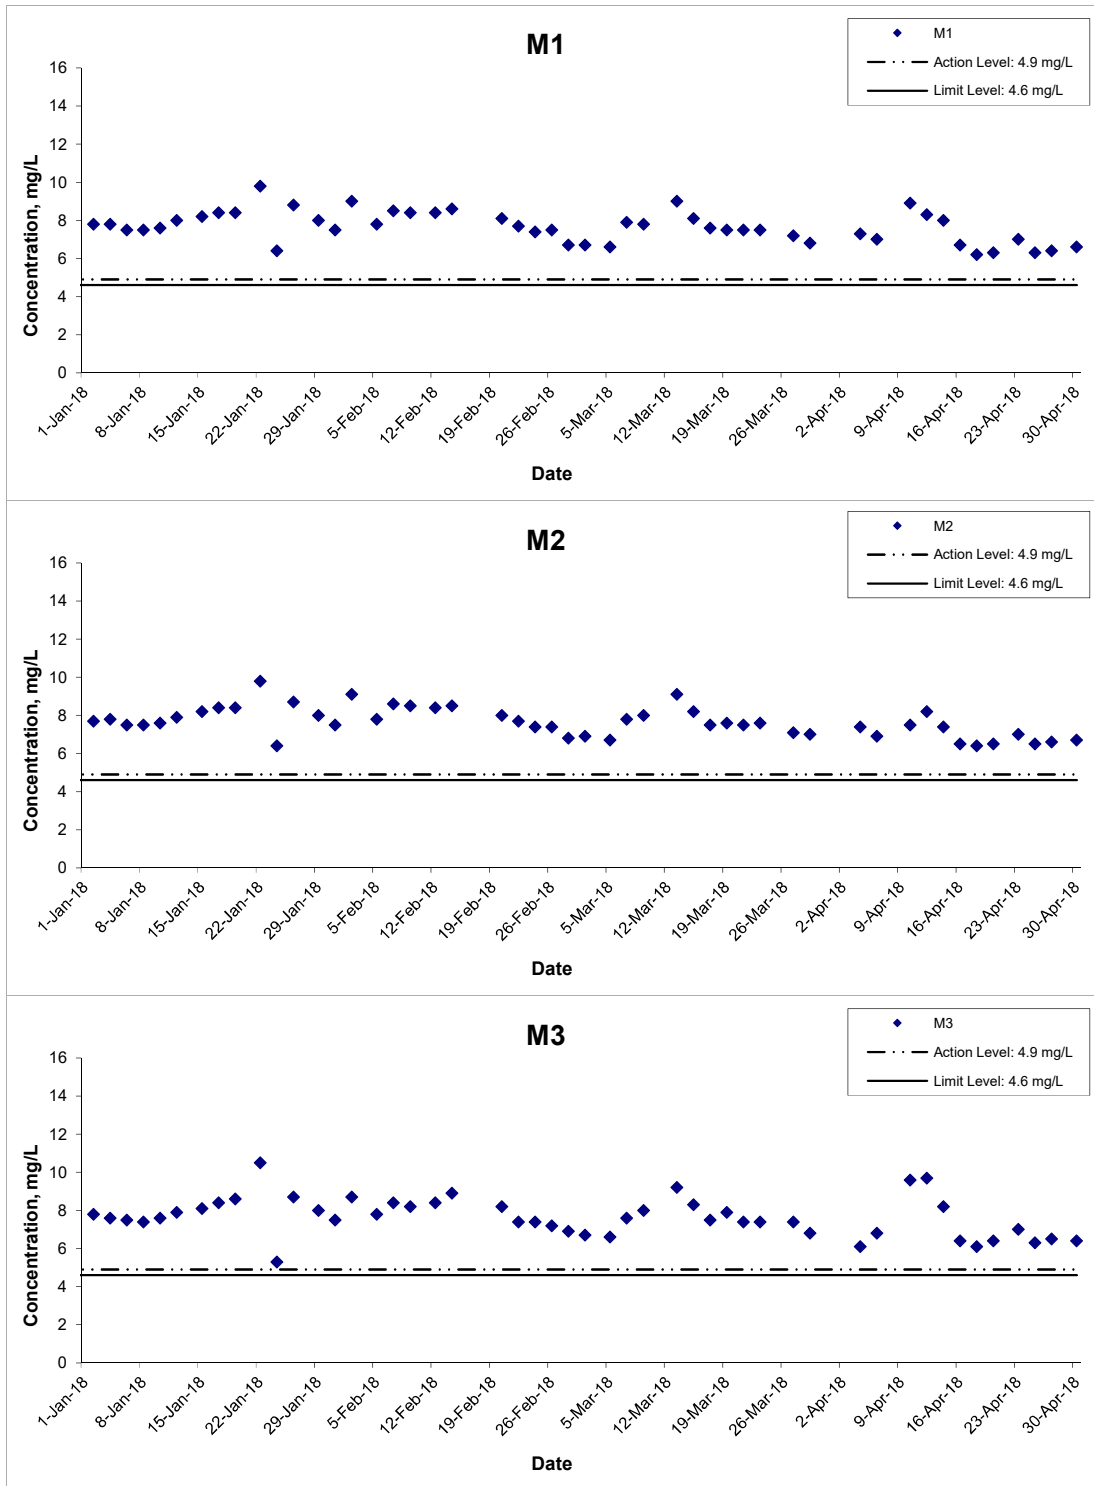

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Depth-averaged) at Mid-Ebb Tide

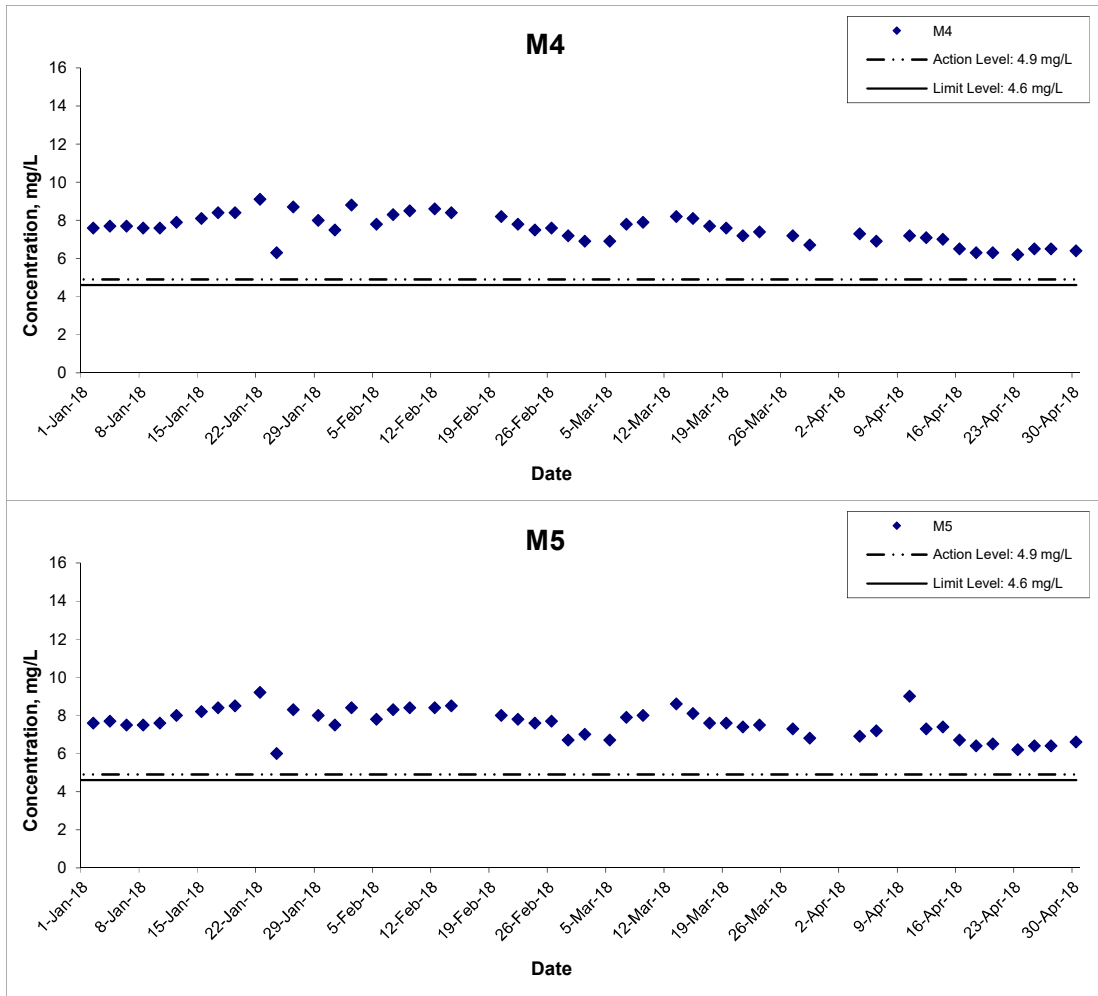

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Depth-averaged) at Mid-Flood Tide

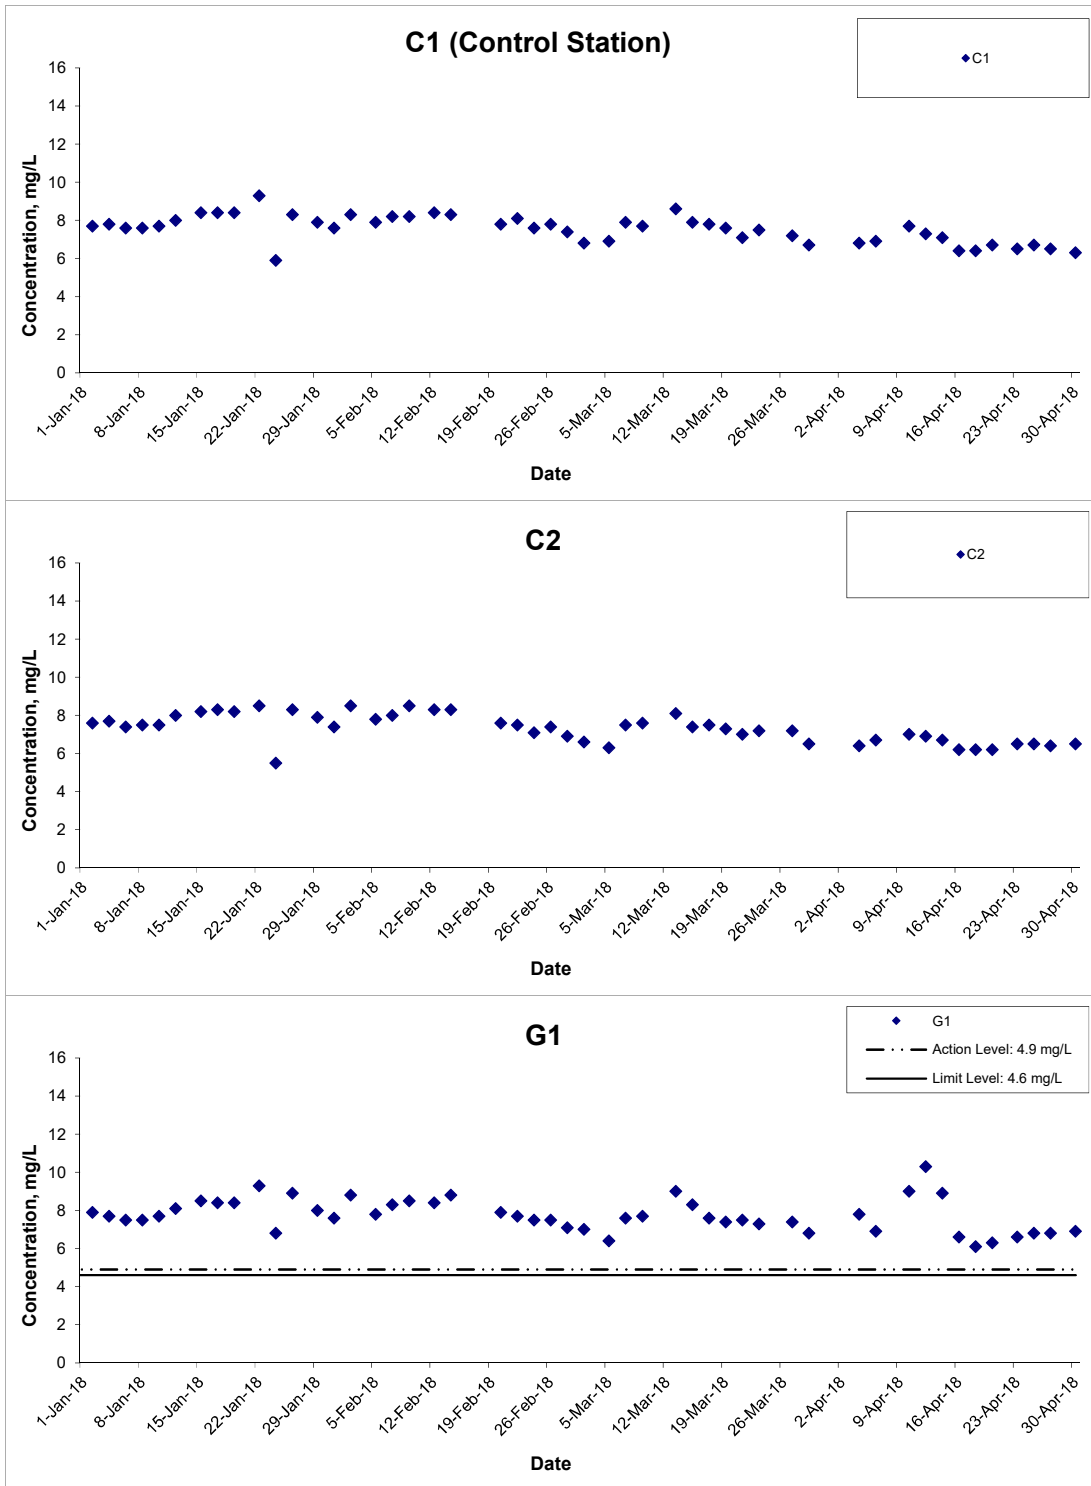

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Depth-averaged) at Mid-Flood Tide

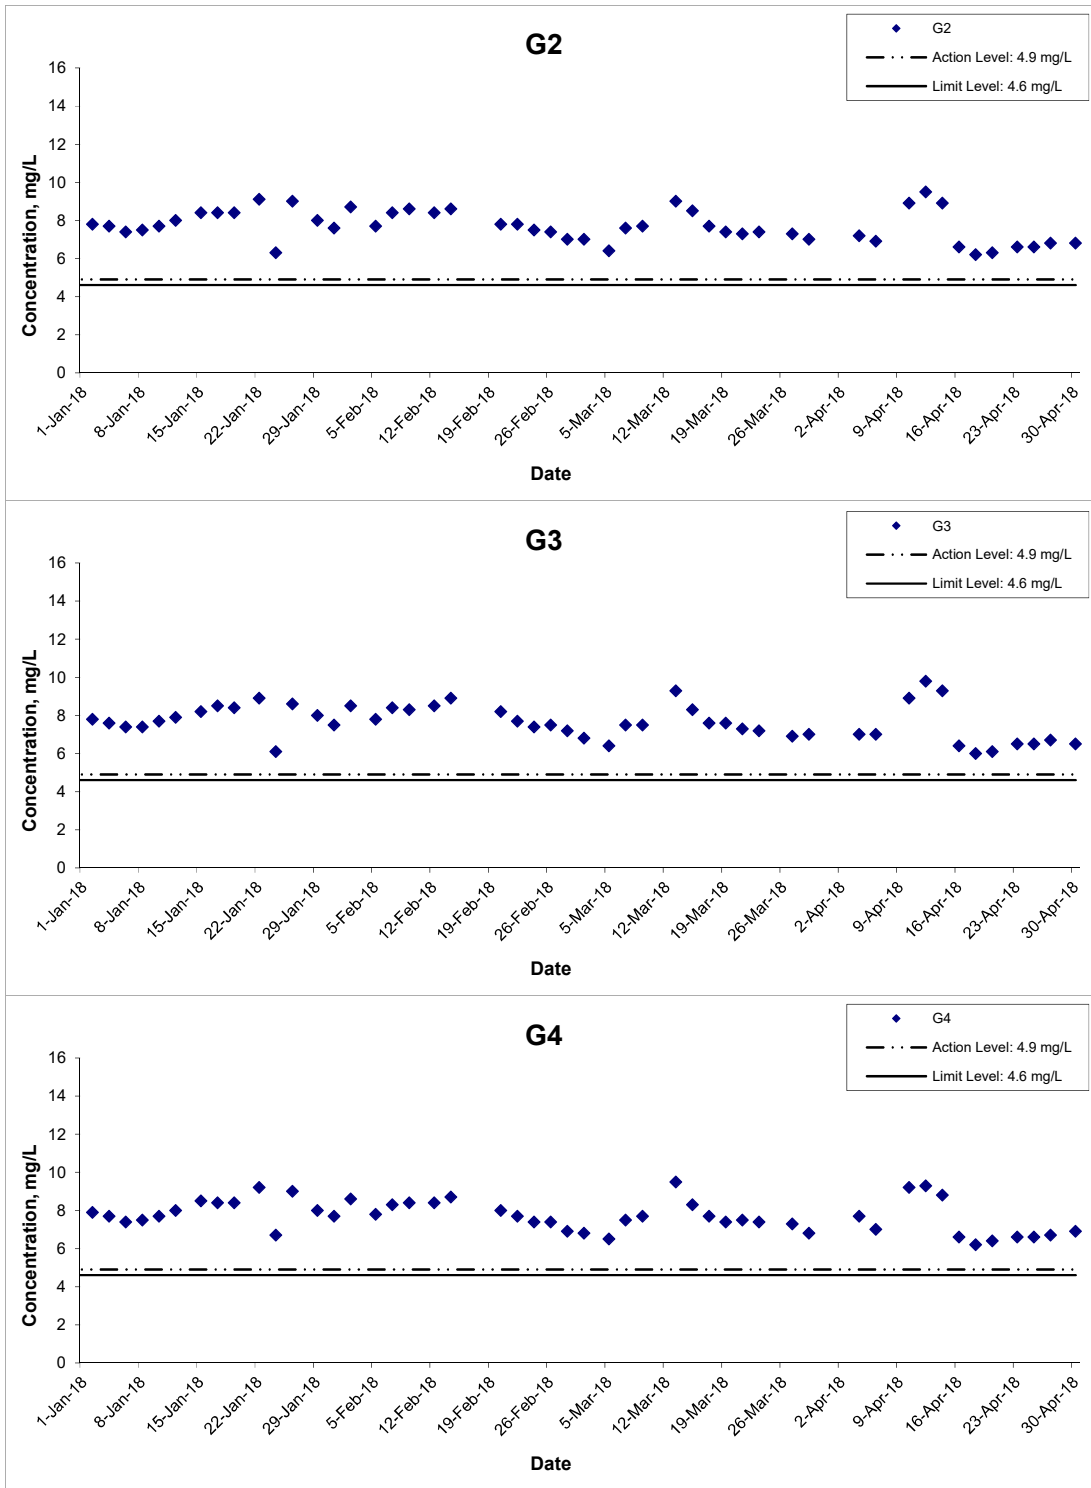

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Depth-averaged) at Mid-Flood Tide

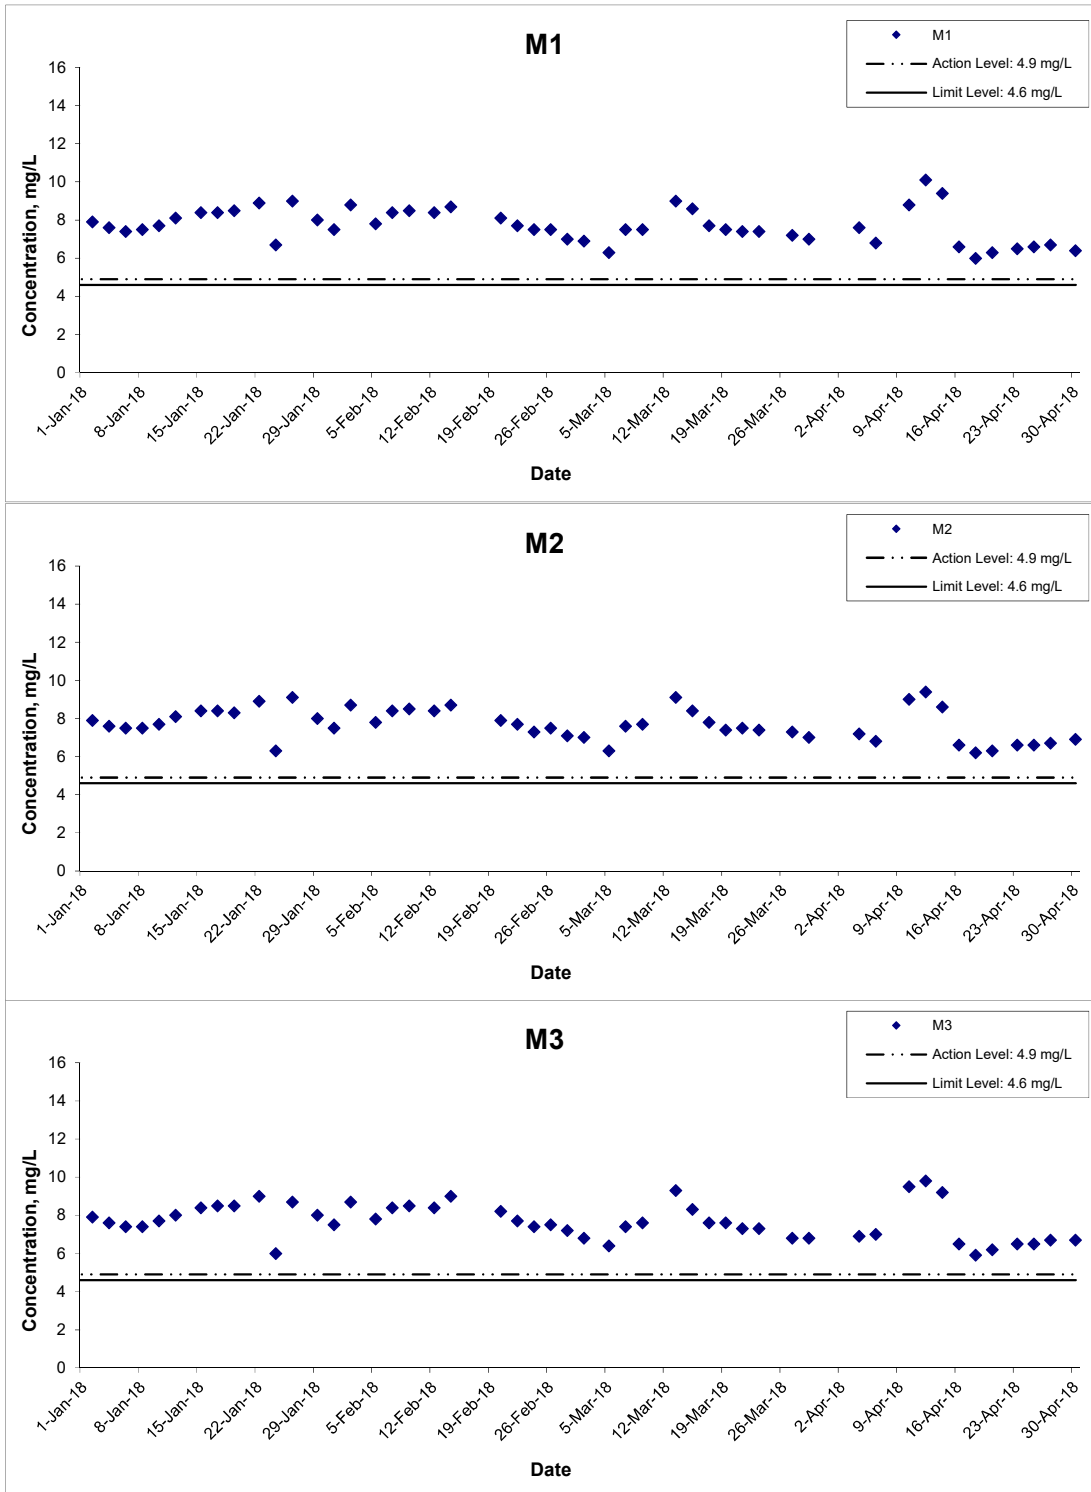

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Depth-averaged) at Mid-Flood Tide

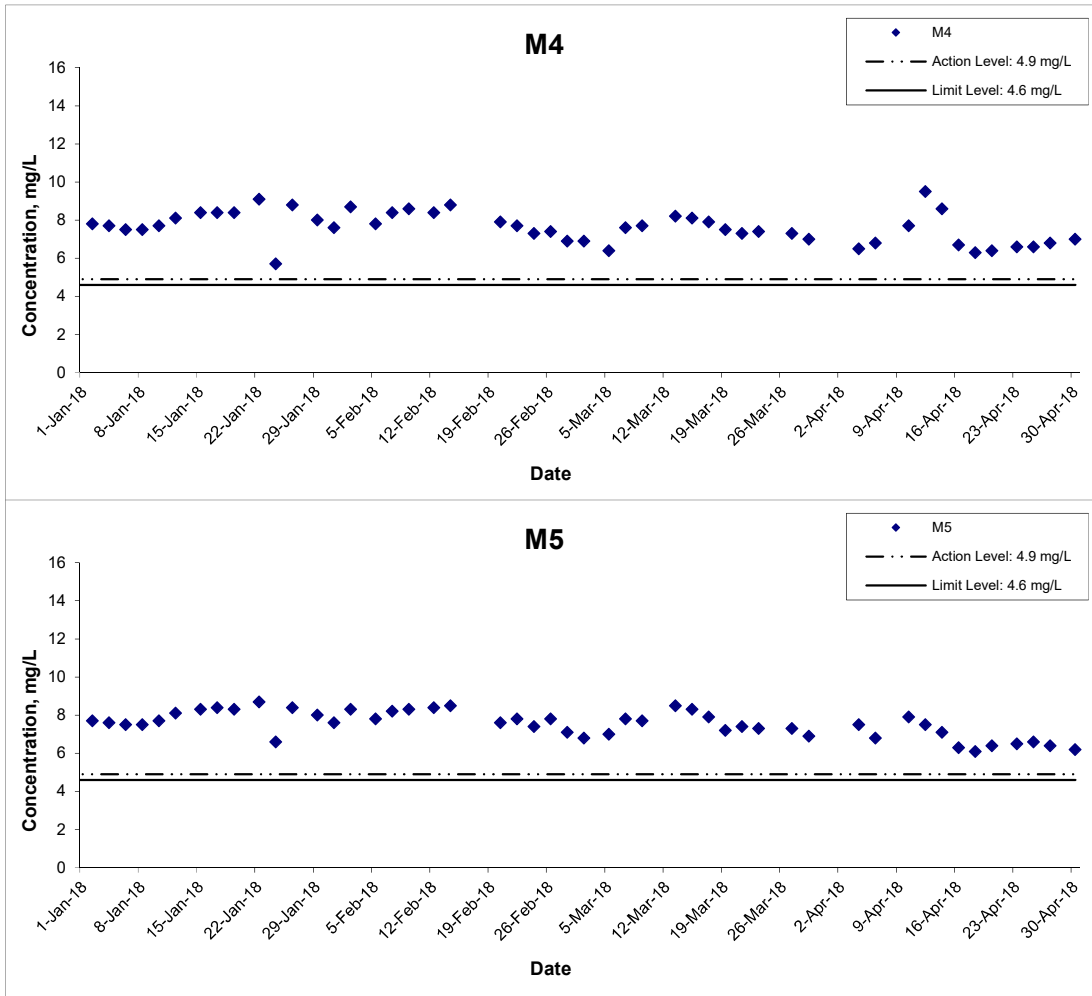

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Bottom) at Mid-Ebb Tide

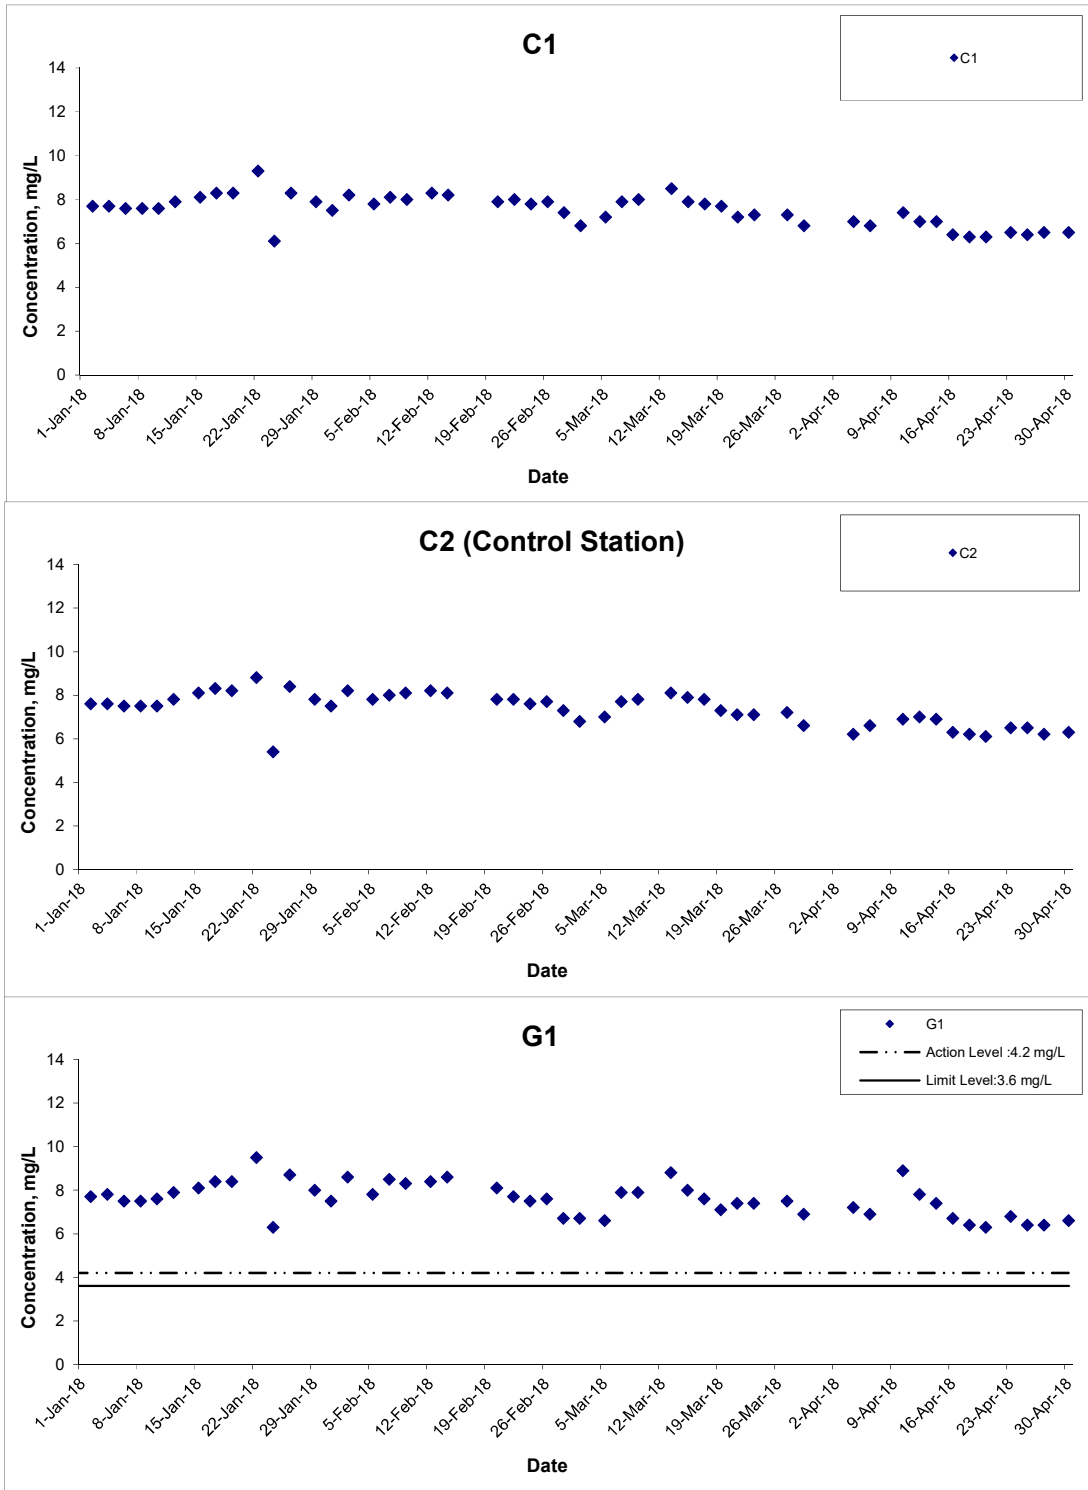


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale	N.T.S	Project No.	MA16034
Date	Apr 18	Appendix	I



Dissolved Oxygen (Bottom) at Mid-Ebb Tide

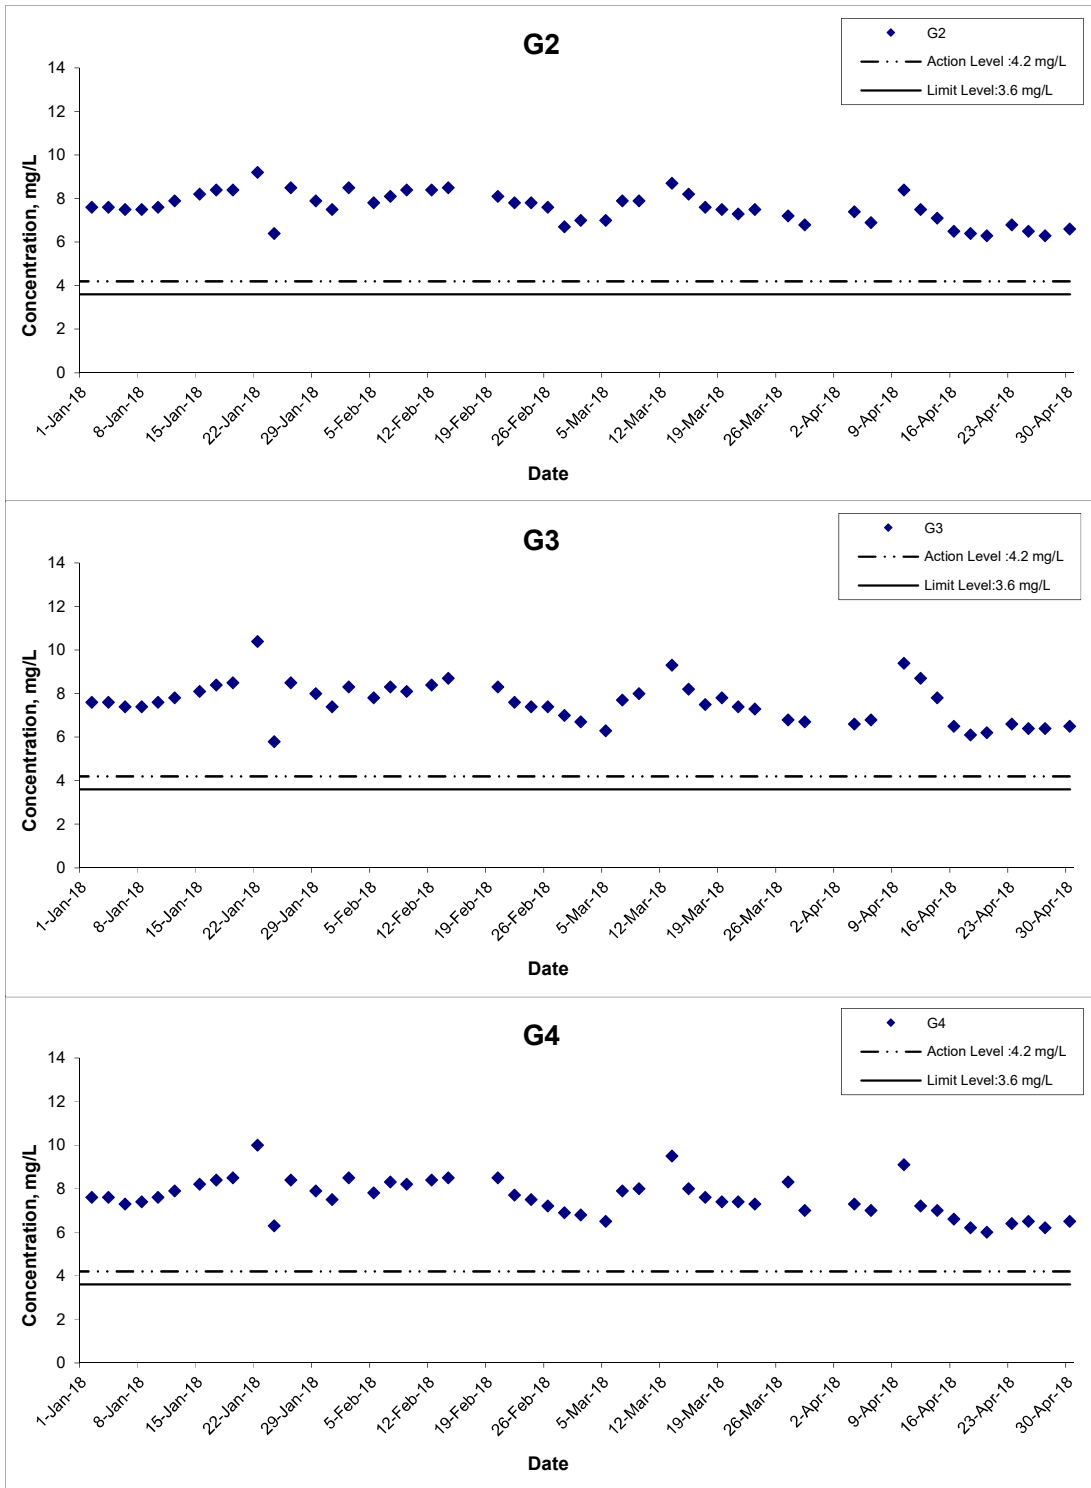


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S
Date Apr 18
Project No. MA16034
Appendix I



Dissolved Oxygen (Bottom) at Mid-Ebb Tide

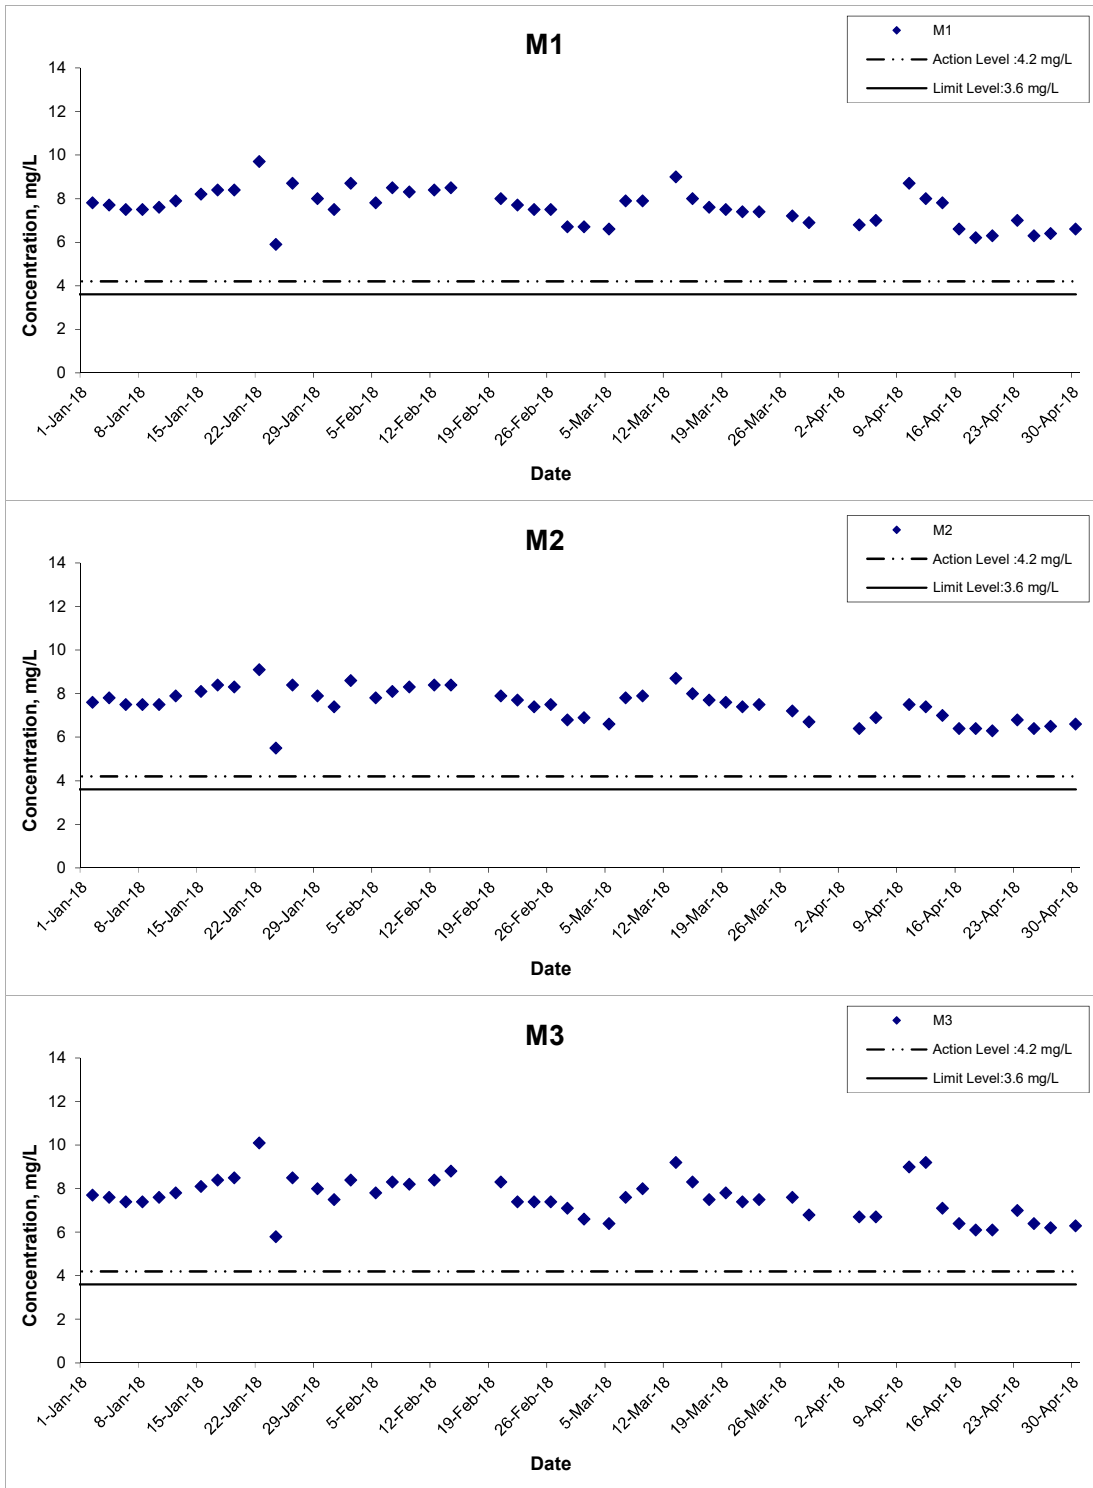


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S
Date Apr 18
Project No. MA16034
Appendix I



Dissolved Oxygen (Bottom) at Mid-Ebb Tide

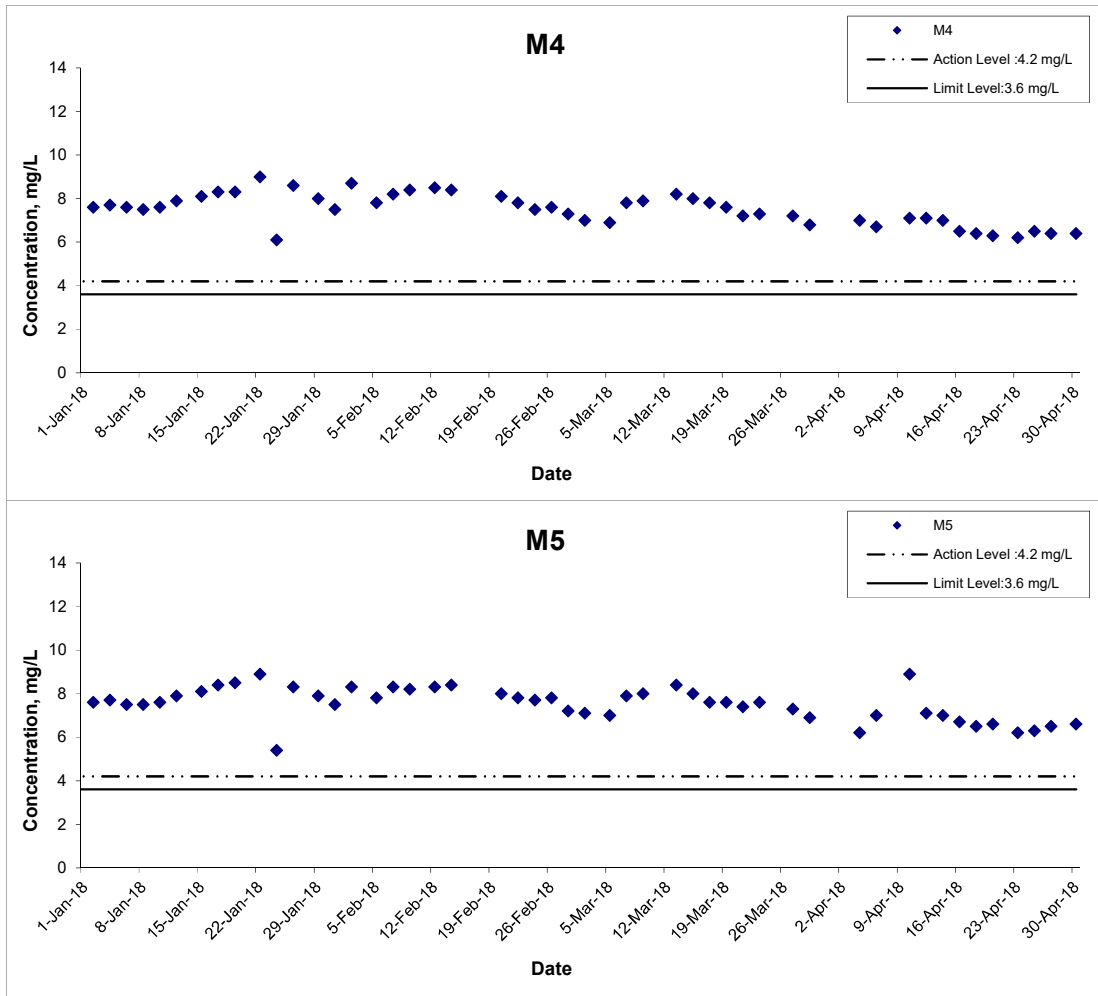

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Bottom) at Mid-Flood Tide

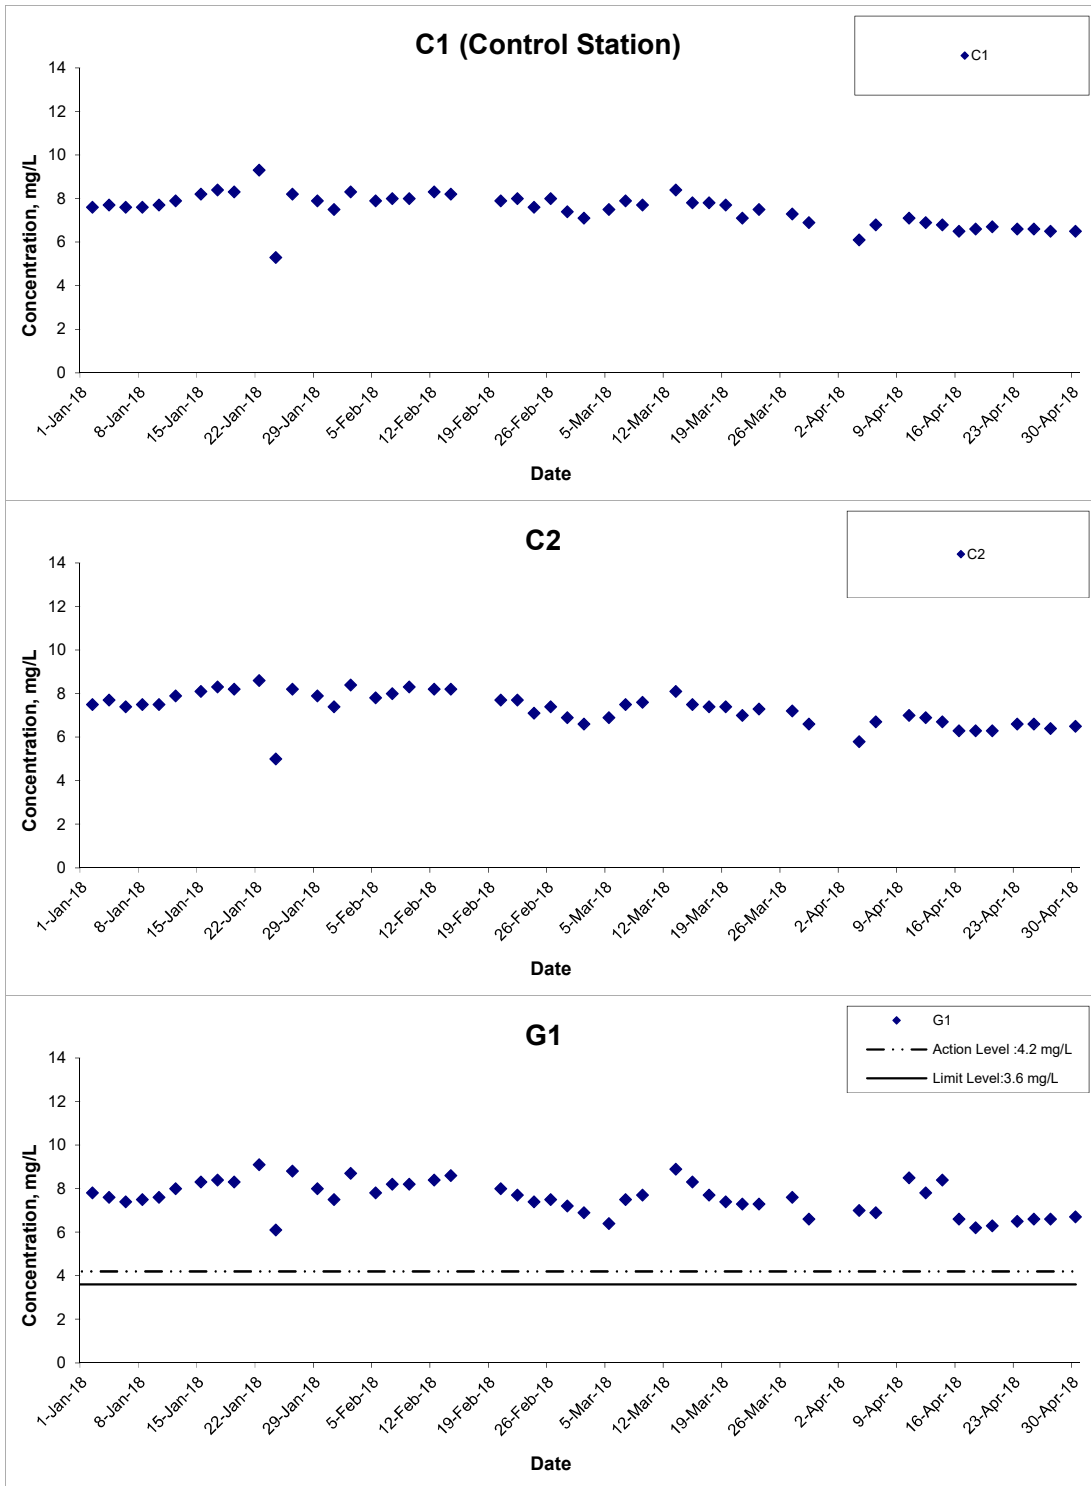

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Bottom) at Mid-Flood Tide



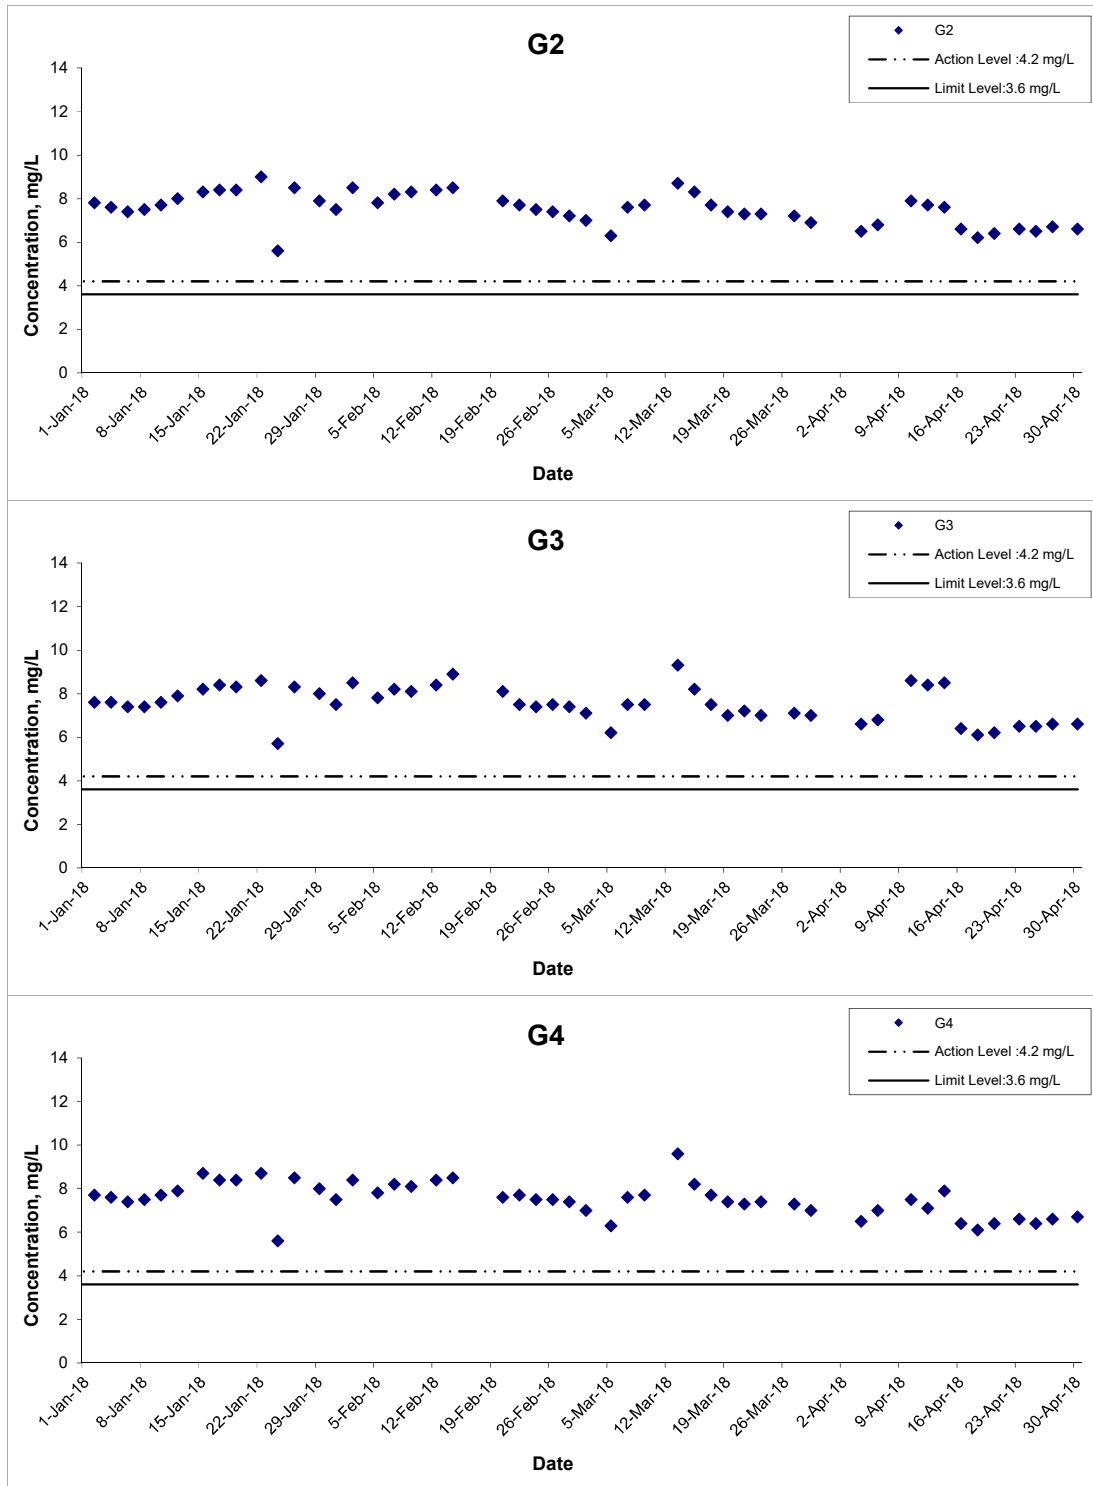


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S
Date Apr 18
Project No. MA16034
Appendix I



Dissolved Oxygen (Bottom) at Mid-Flood Tide

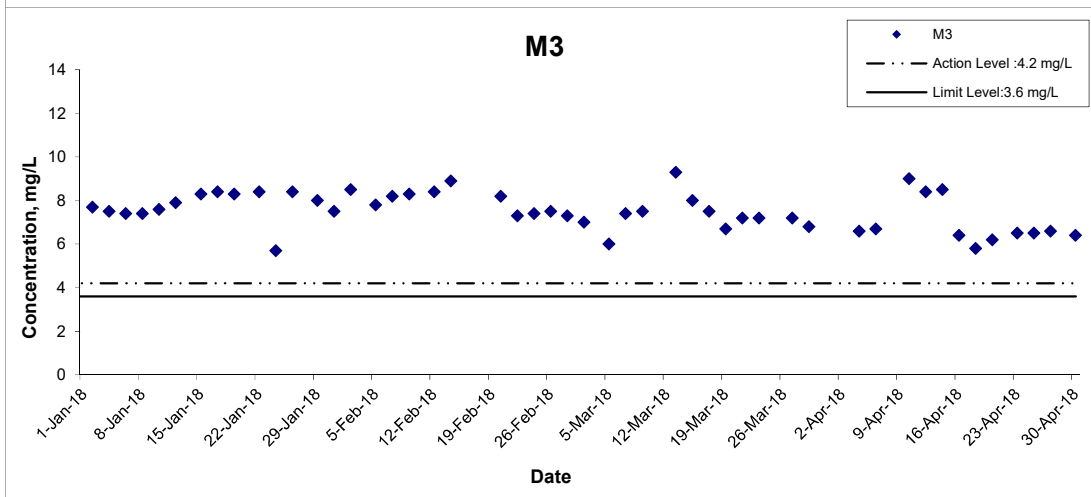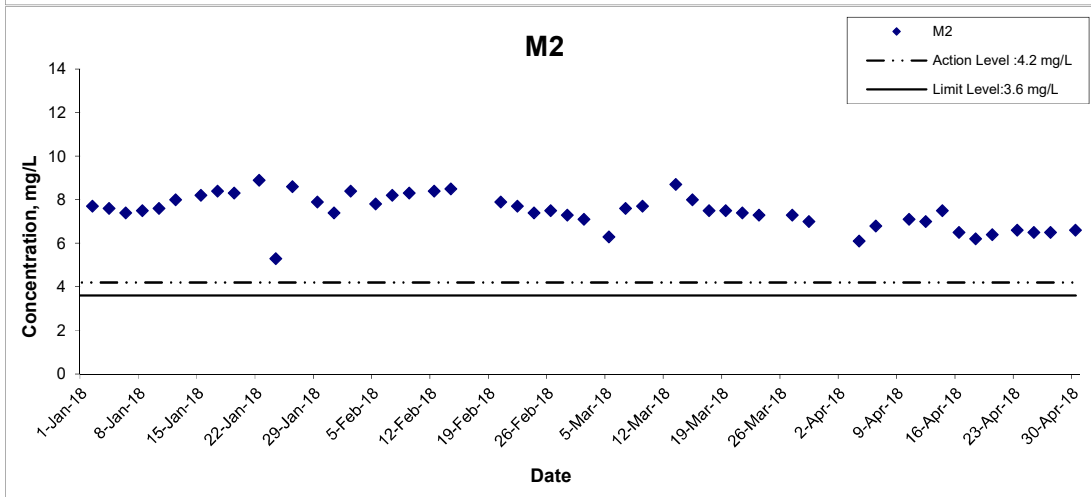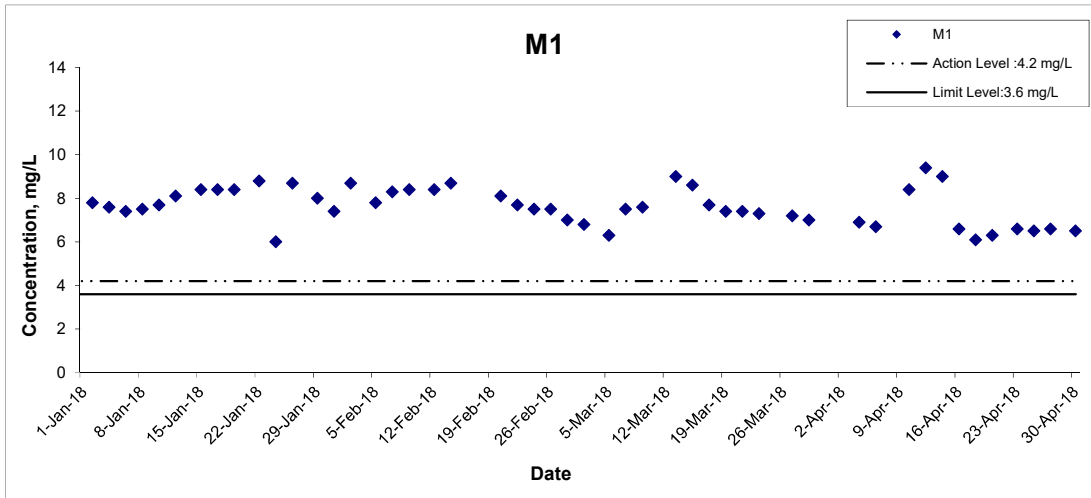

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Bottom) at Mid-Flood Tide

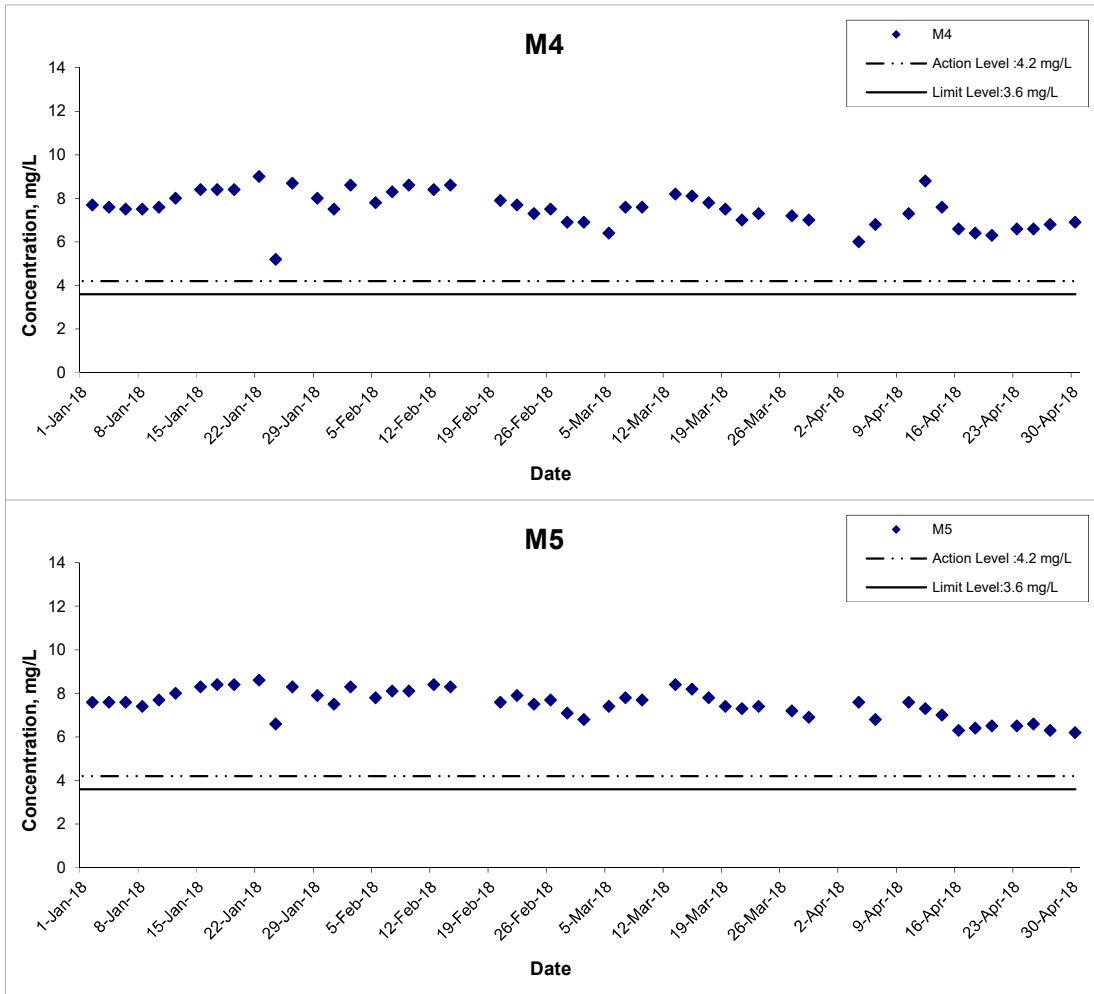

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Dissolved Oxygen (Intake Level of WSD Salt Water Intake) at Mid-Ebb Tide

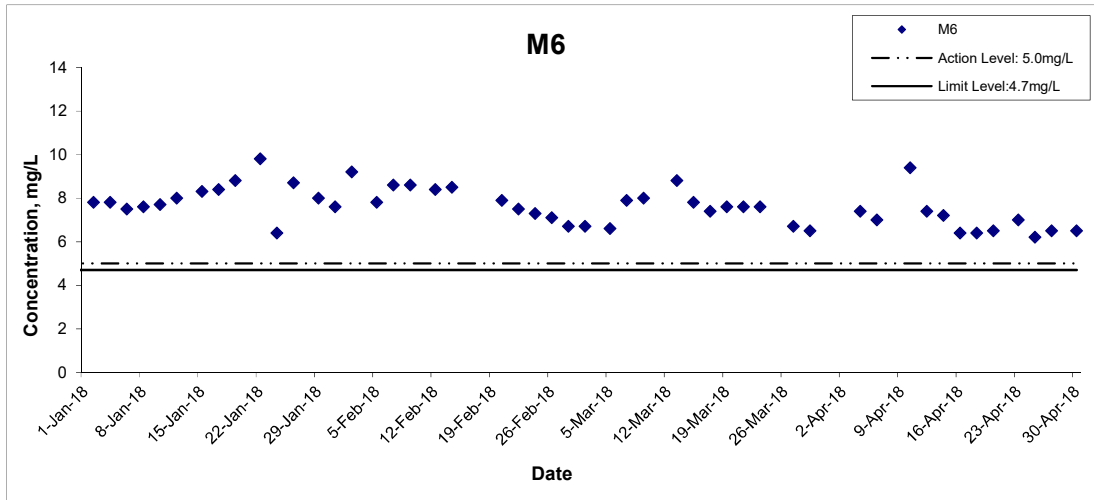


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S
 Date Apr 18

Project No. MA16034
 Appendix I



Dissolved Oxygen (Intake Level of WSD Salt Water Intake) at Mid-Flood Tide

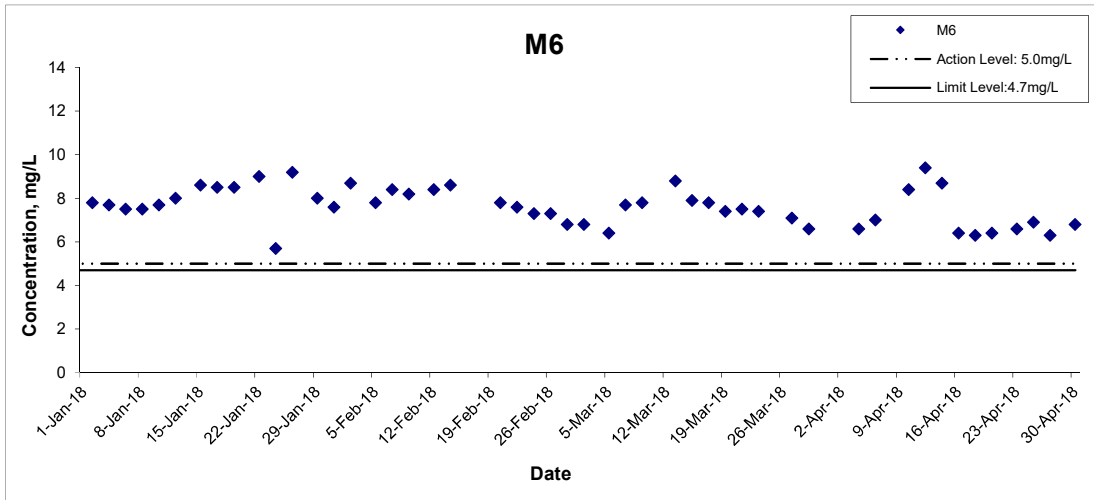


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
 Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S
 Date Apr 18

Project No. MA16034
 Appendix I



Turbidity (Depth-averaged) at Mid-Ebb Tide

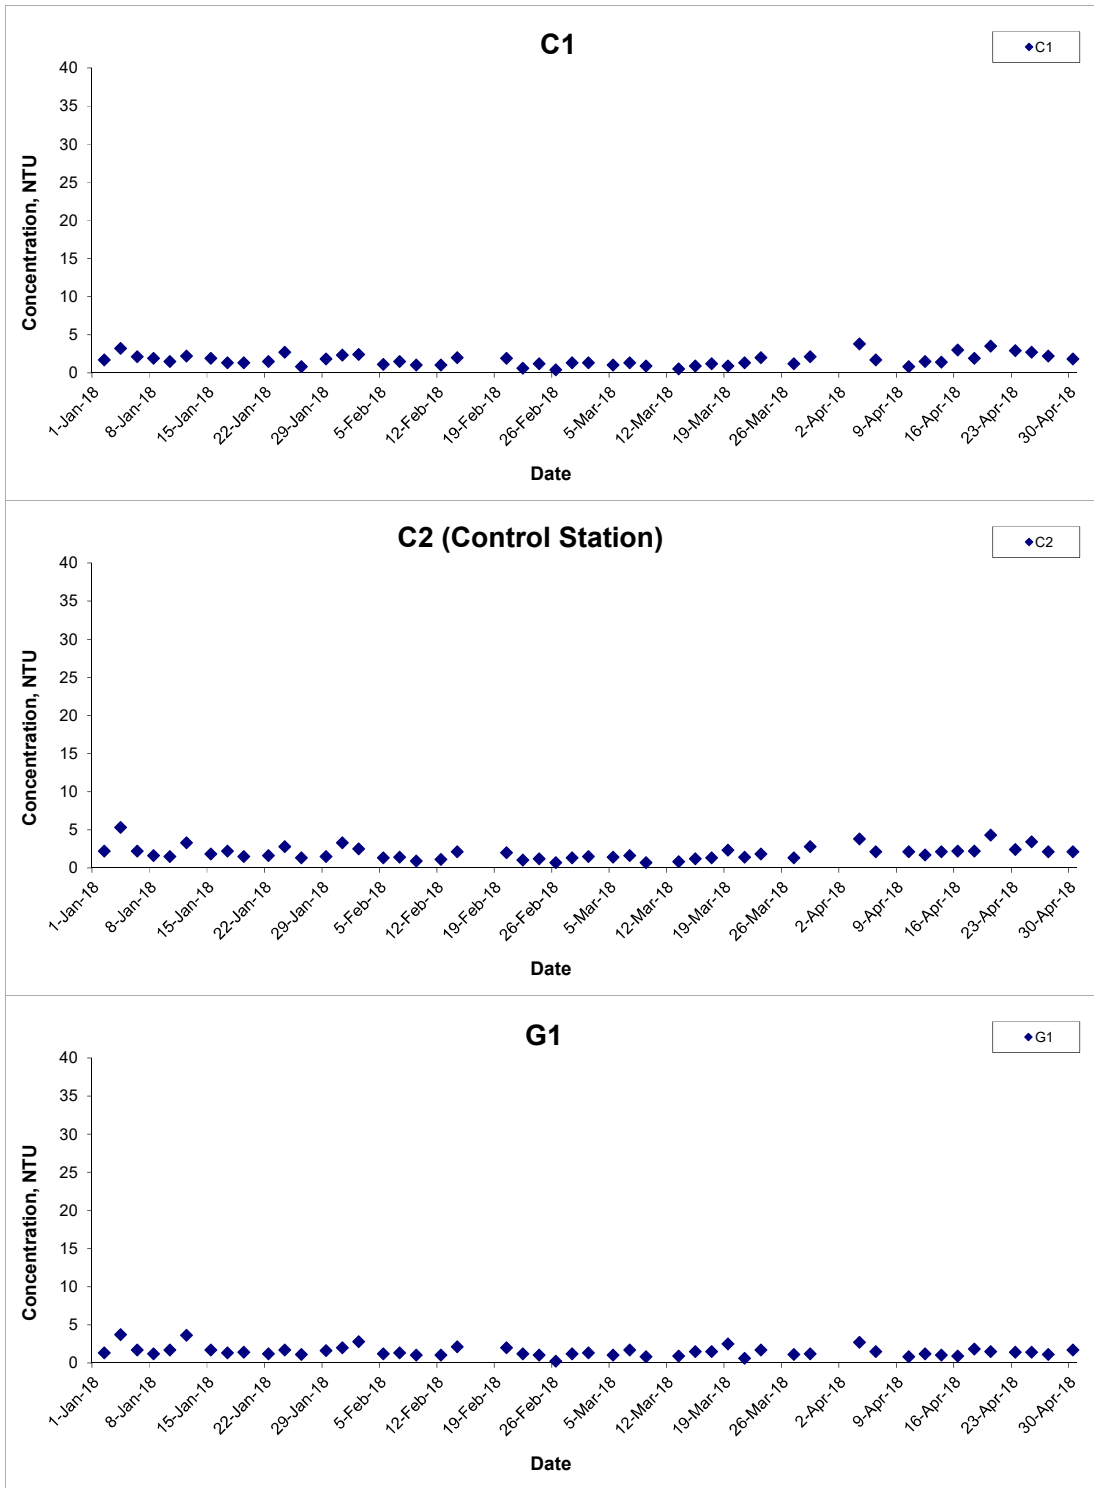

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Depth-averaged) at Mid-Ebb Tide

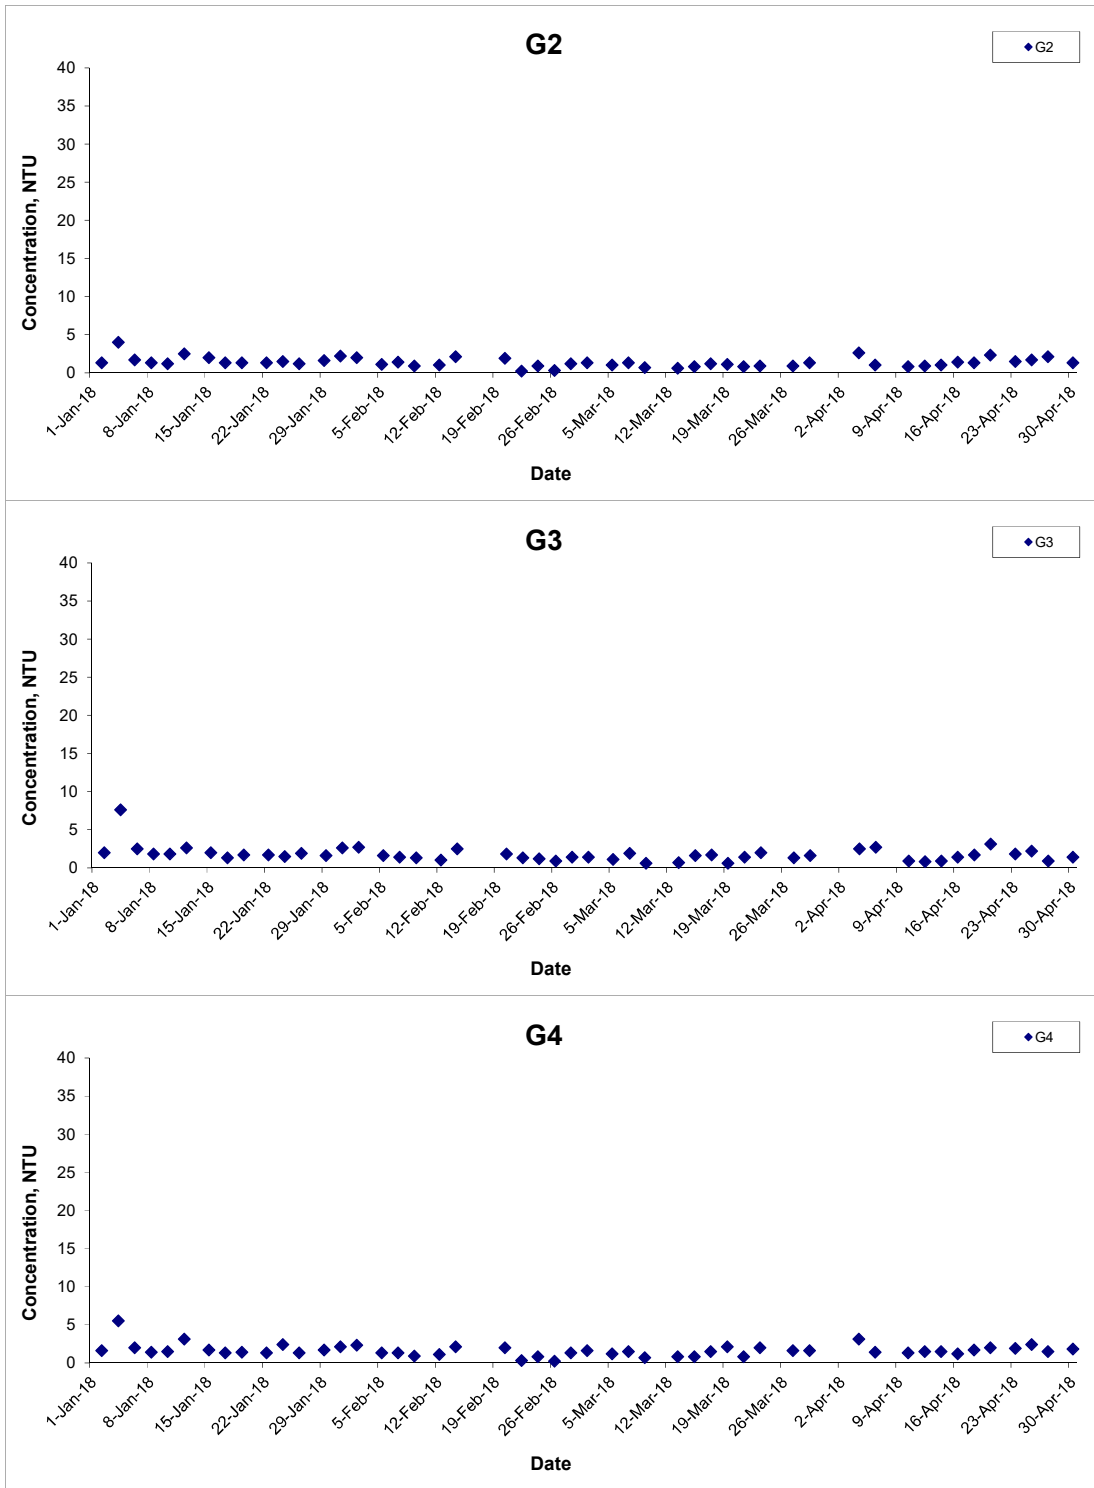

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Depth-averaged) at Mid-Ebb Tide

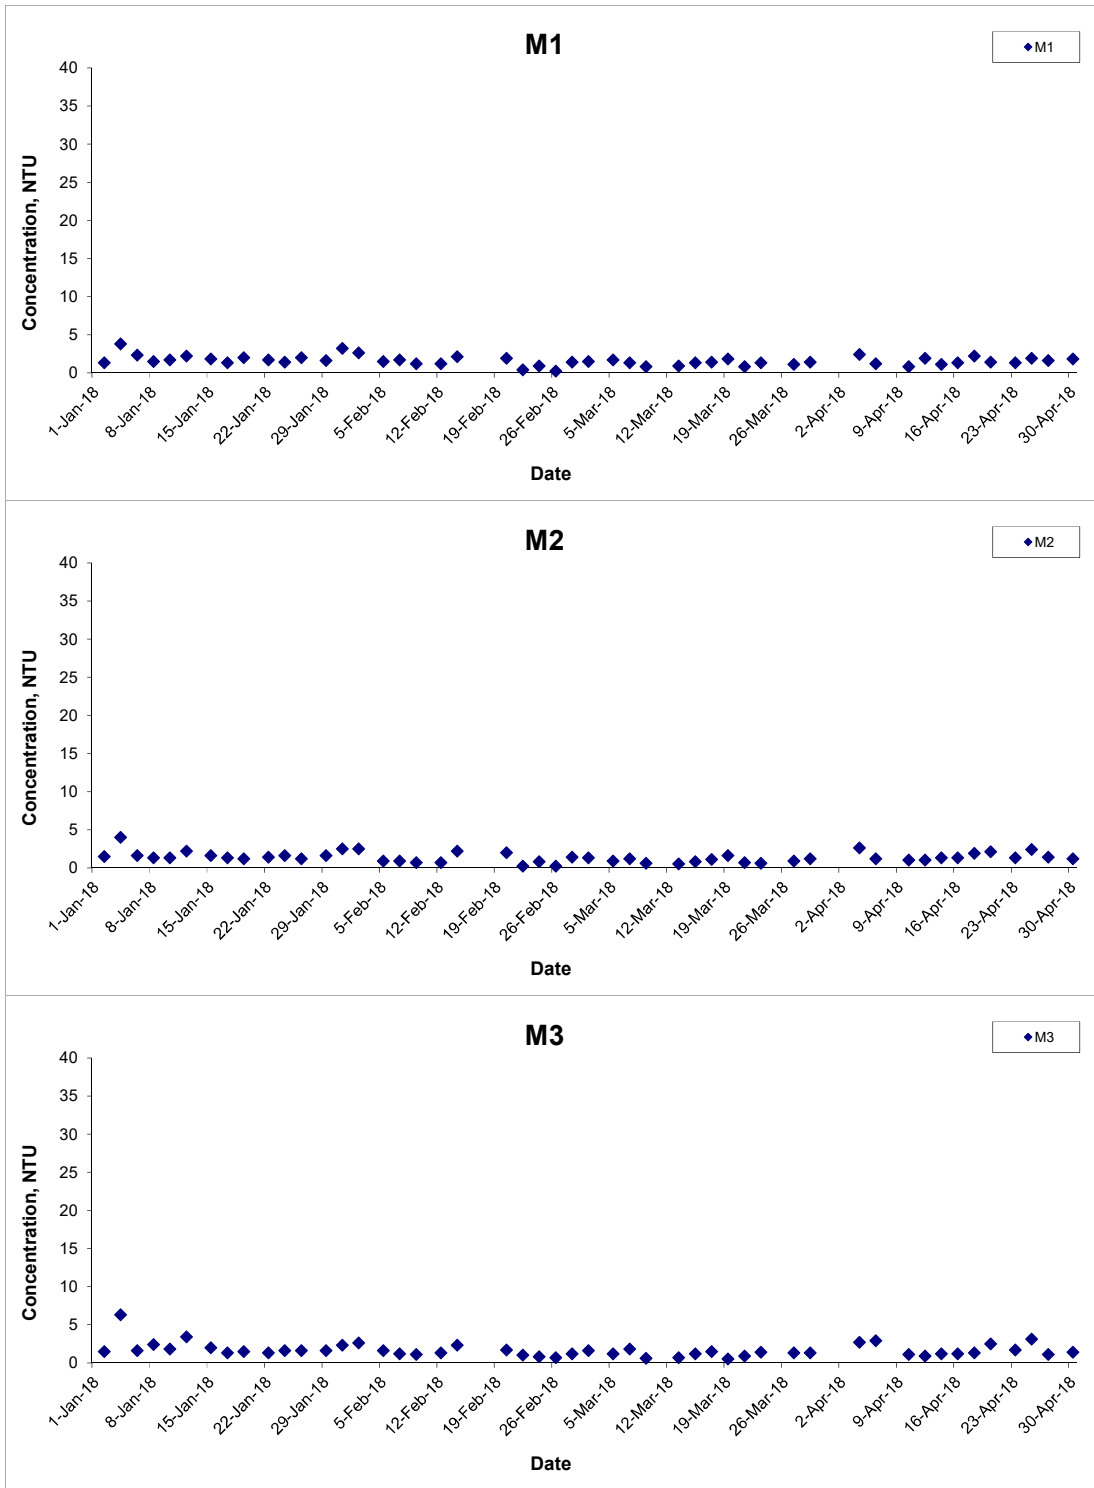

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Depth-averaged) at Mid-Ebb Tide

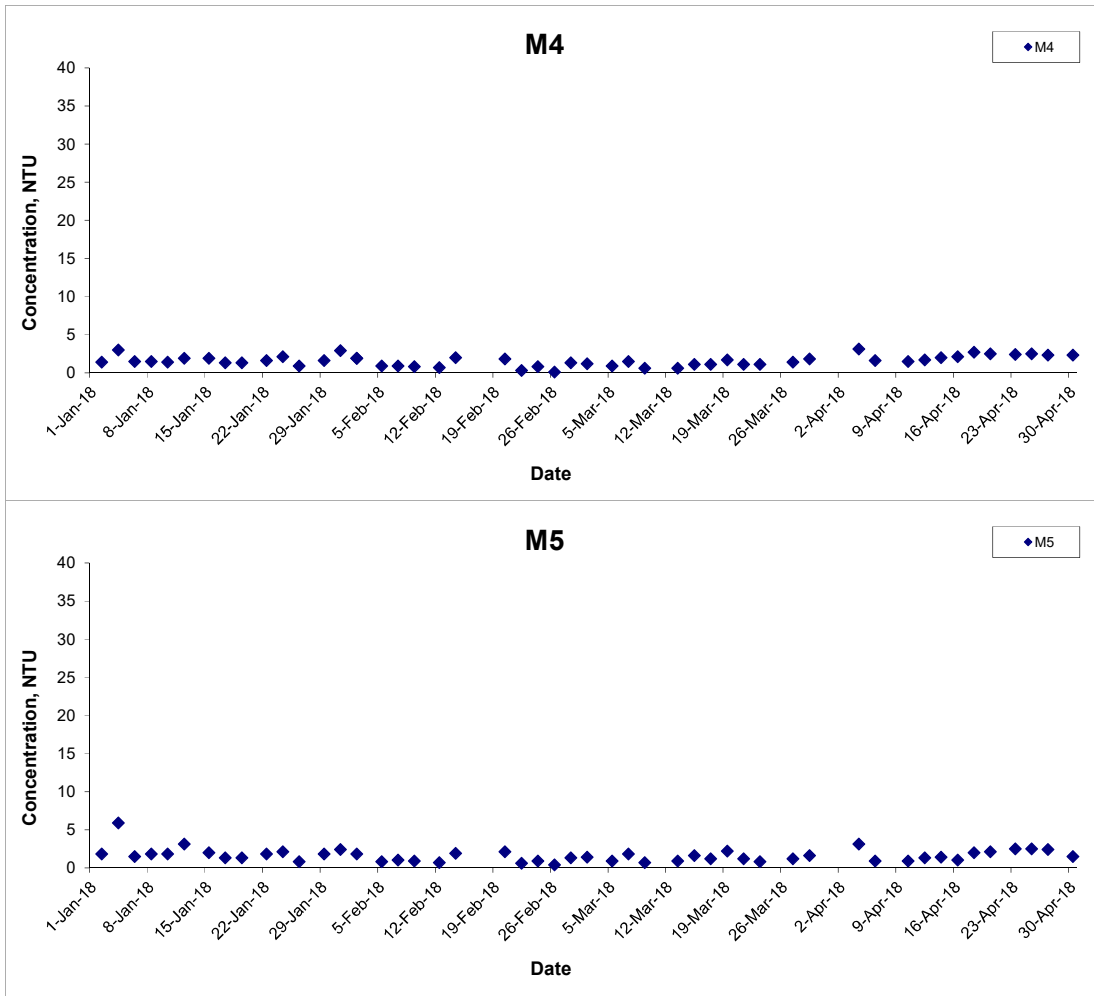

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Depth-averaged) at Mid-Flood Tide

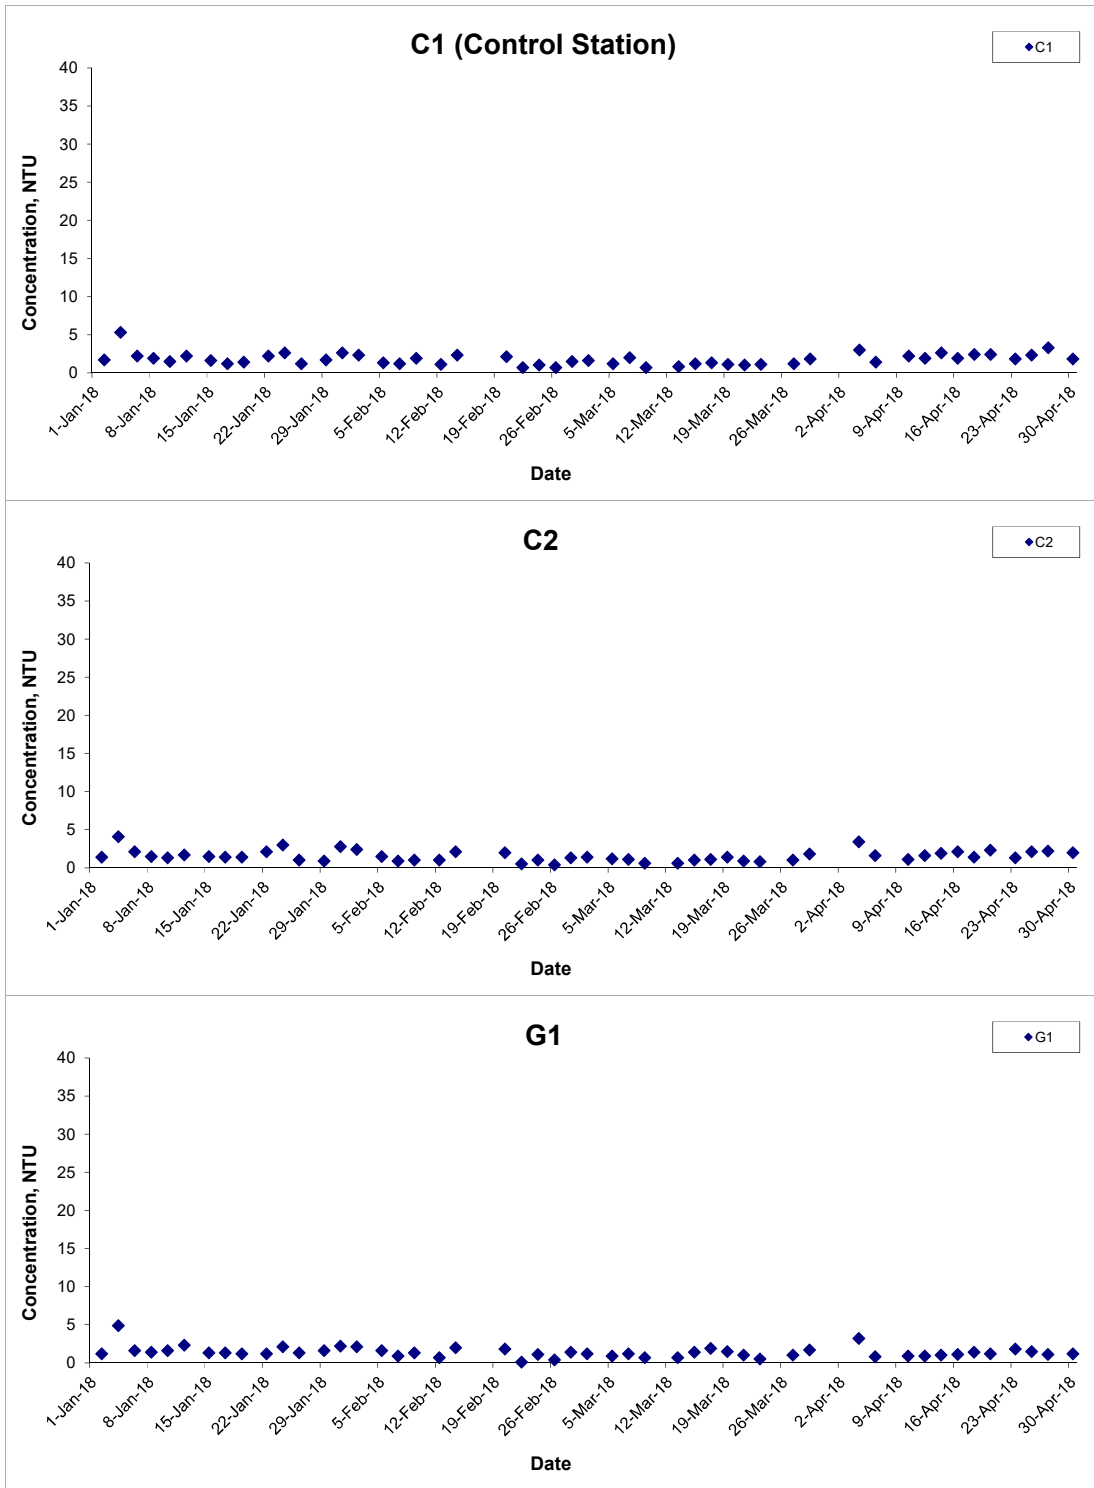

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Depth-averaged) at Mid-Flood Tide

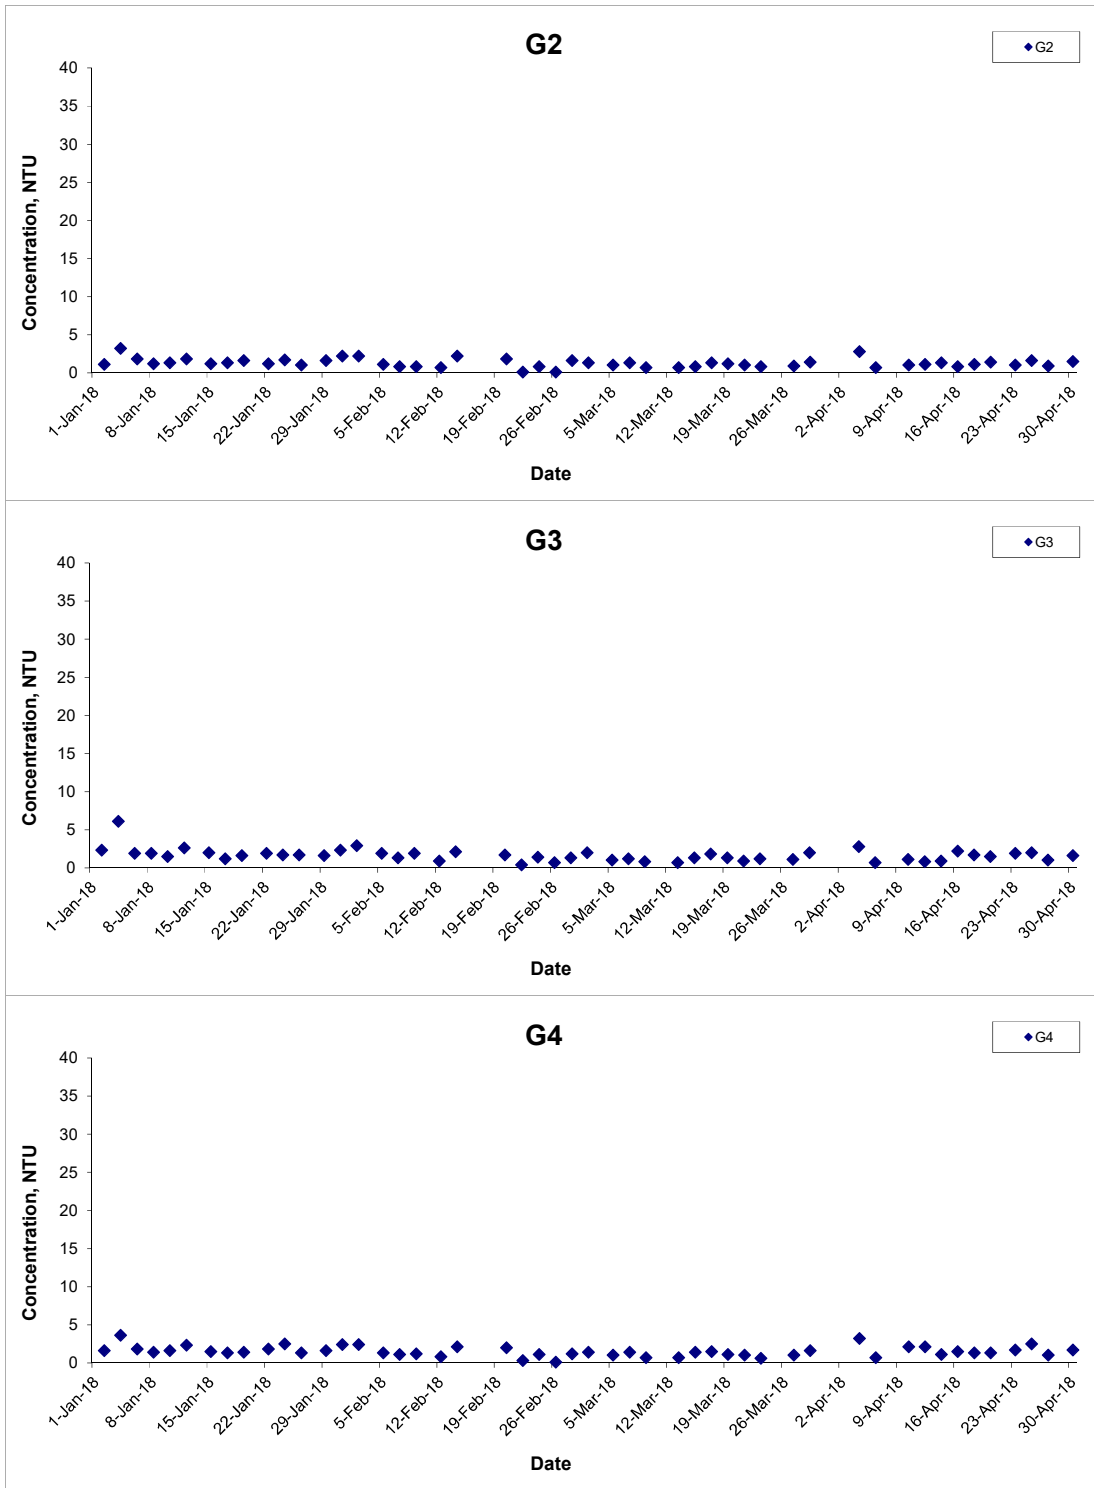

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Depth-averaged) at Mid-Flood Tide

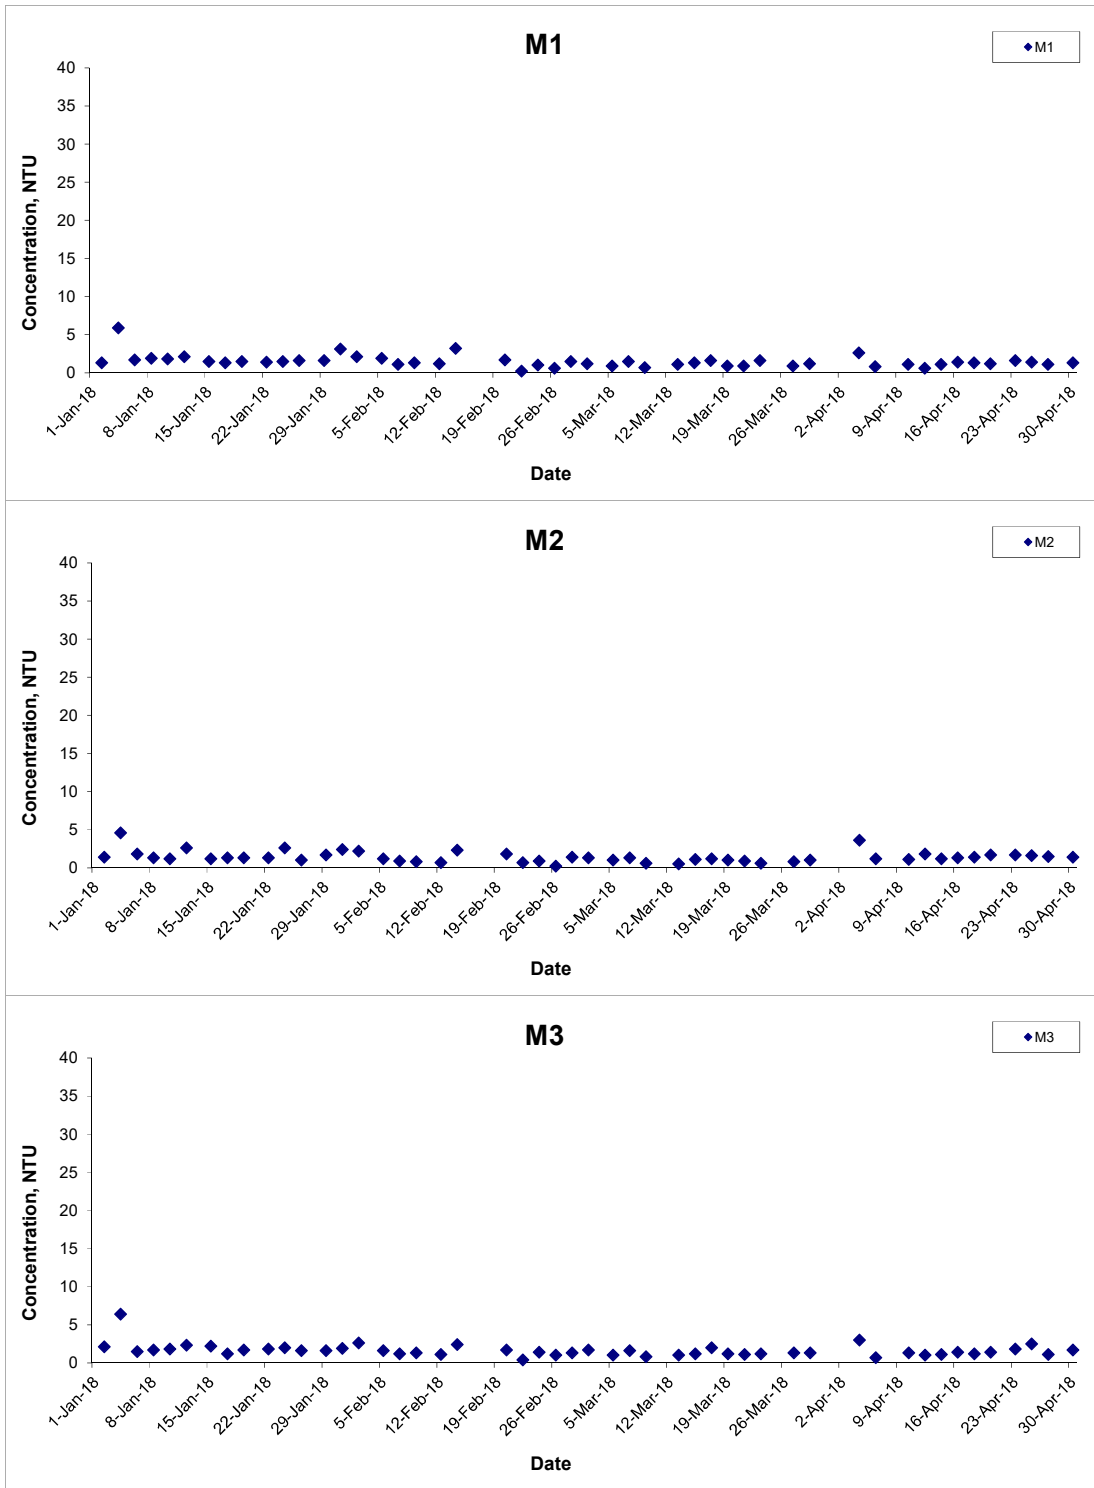

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Depth-averaged) at Mid-Flood Tide

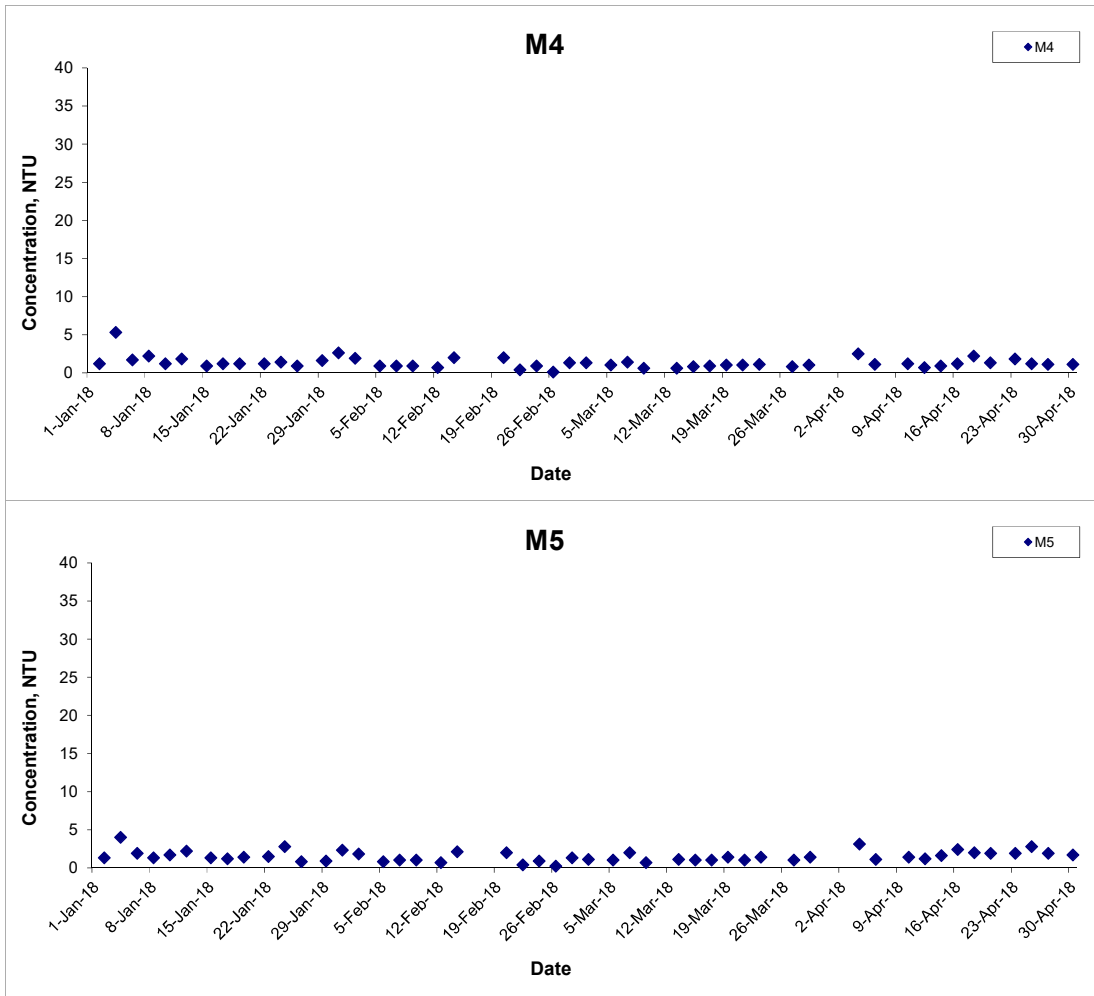

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Ebb Tide

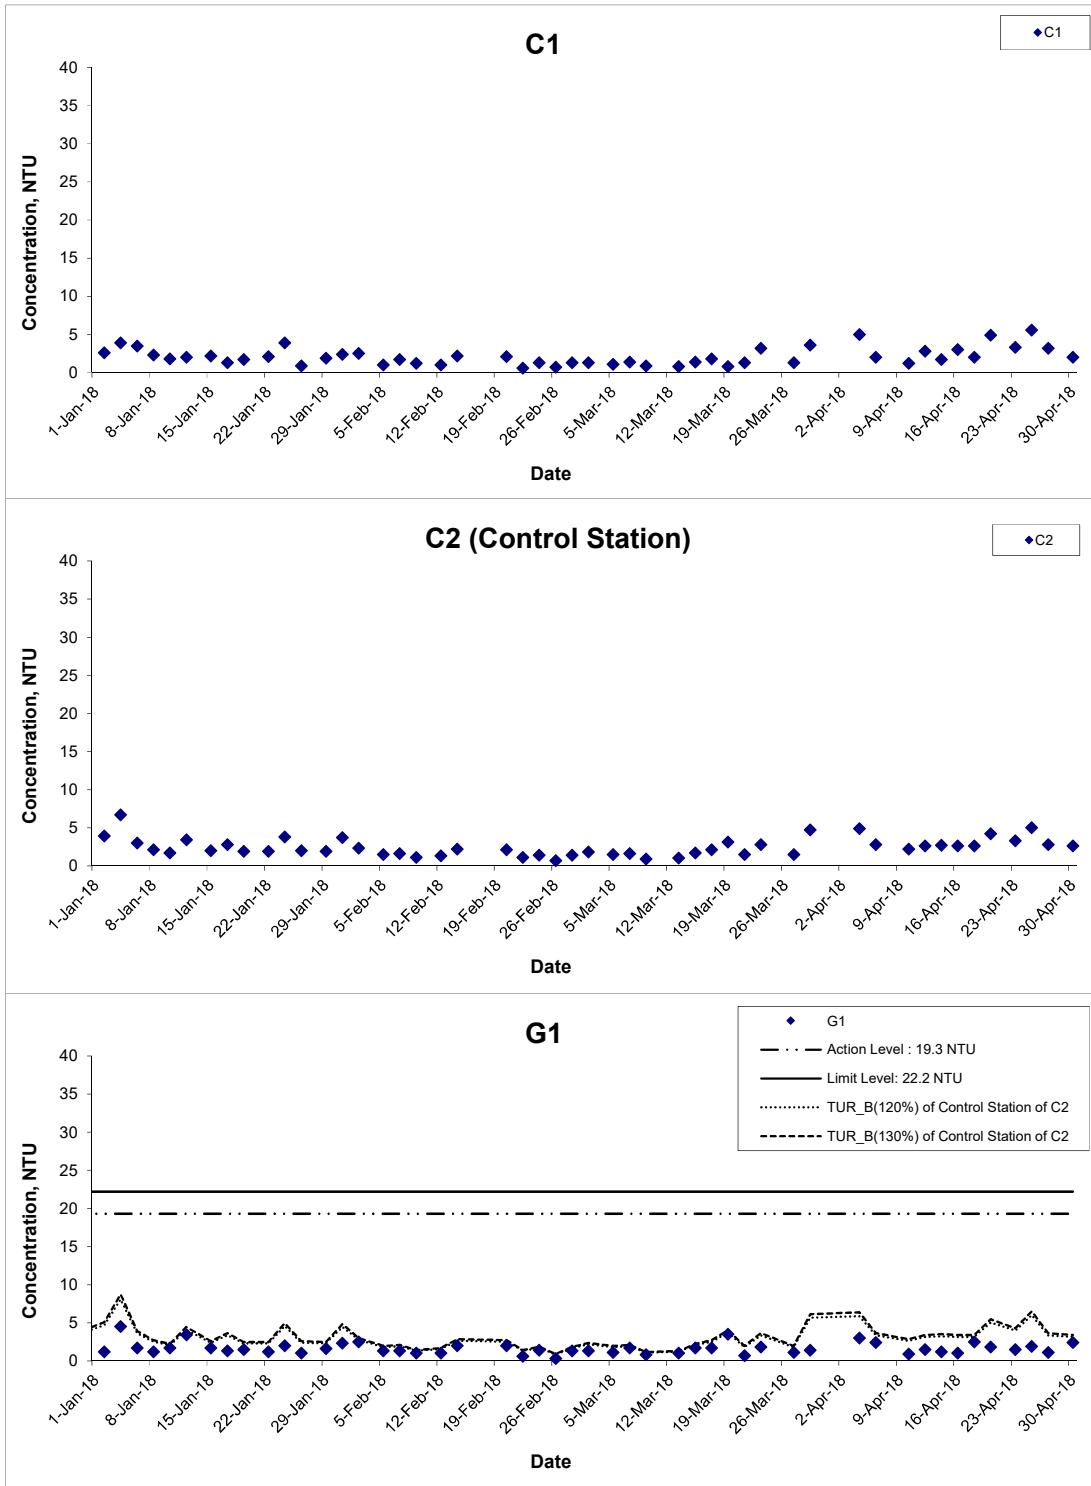

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Ebb Tide

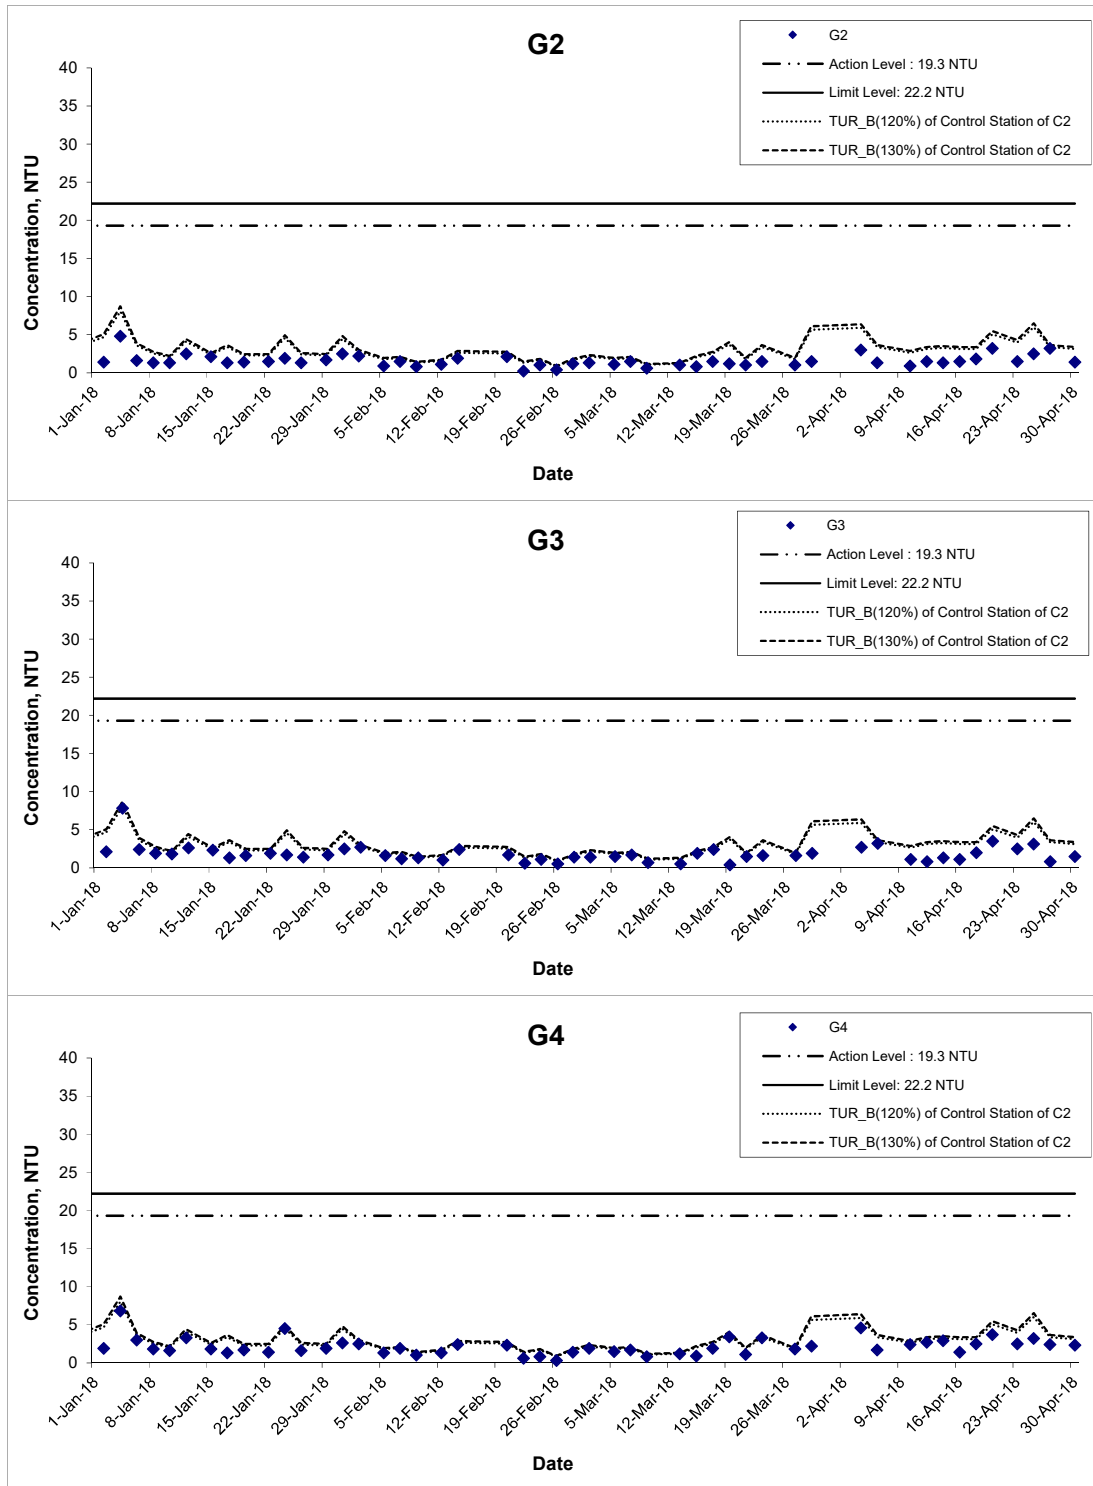

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Ebb Tide

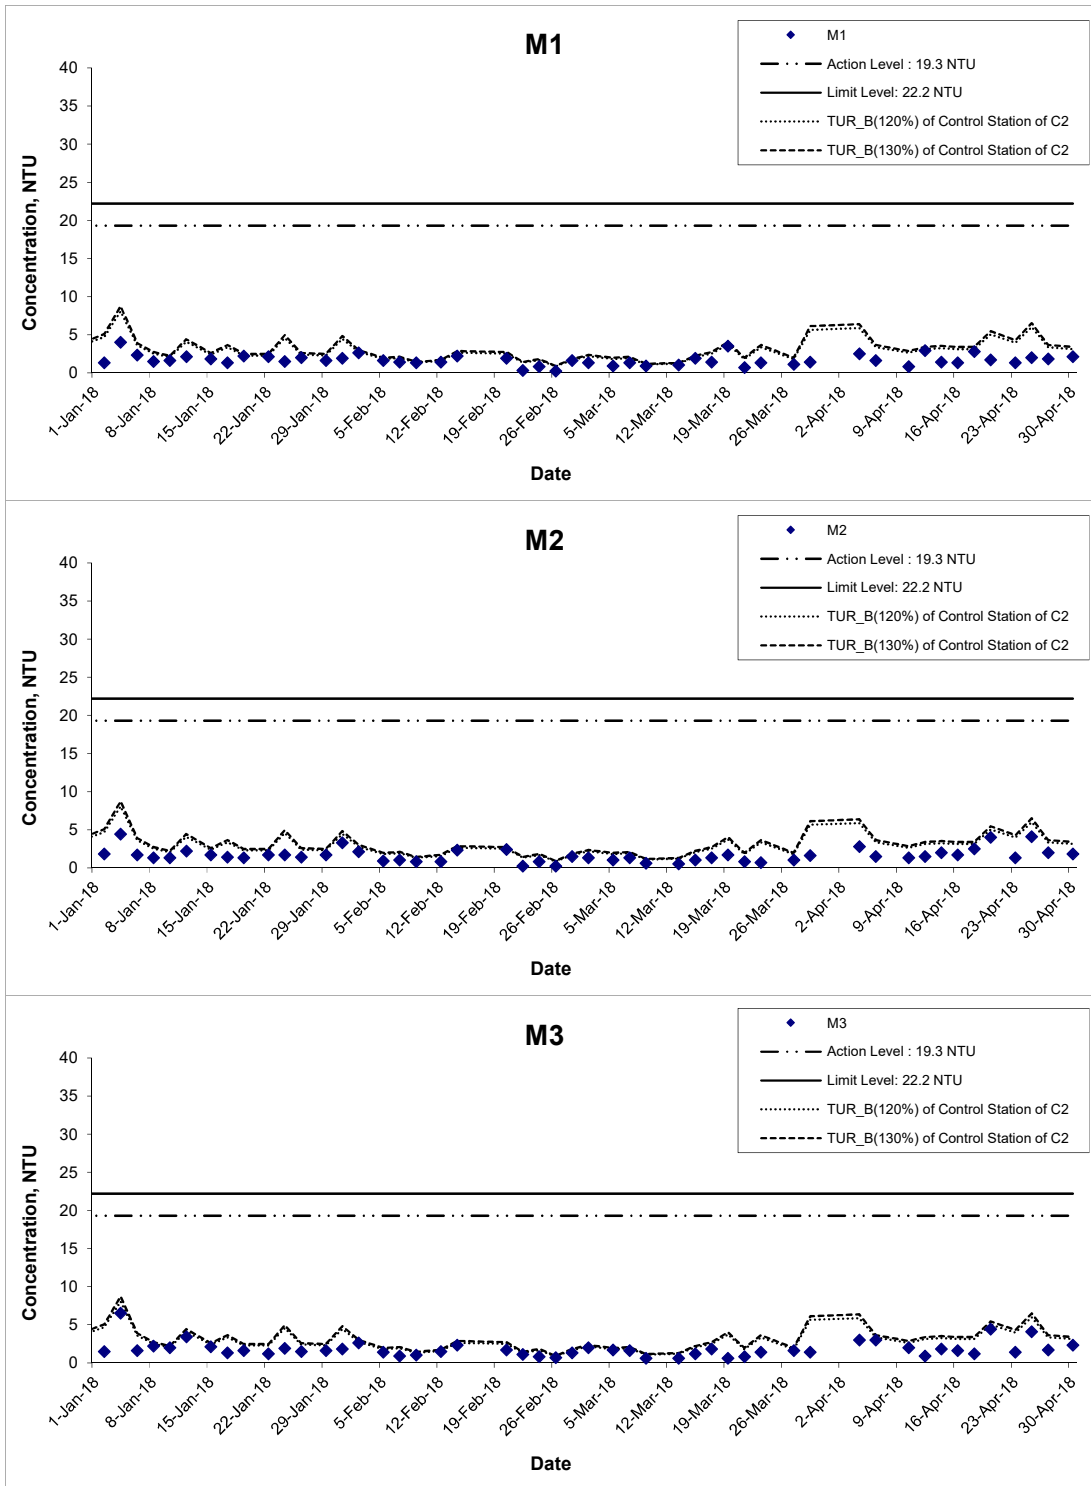


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S
Date Apr 18
Project No. MA16034
Appendix I



Turbidity (Bottom) at Mid-Ebb Tide

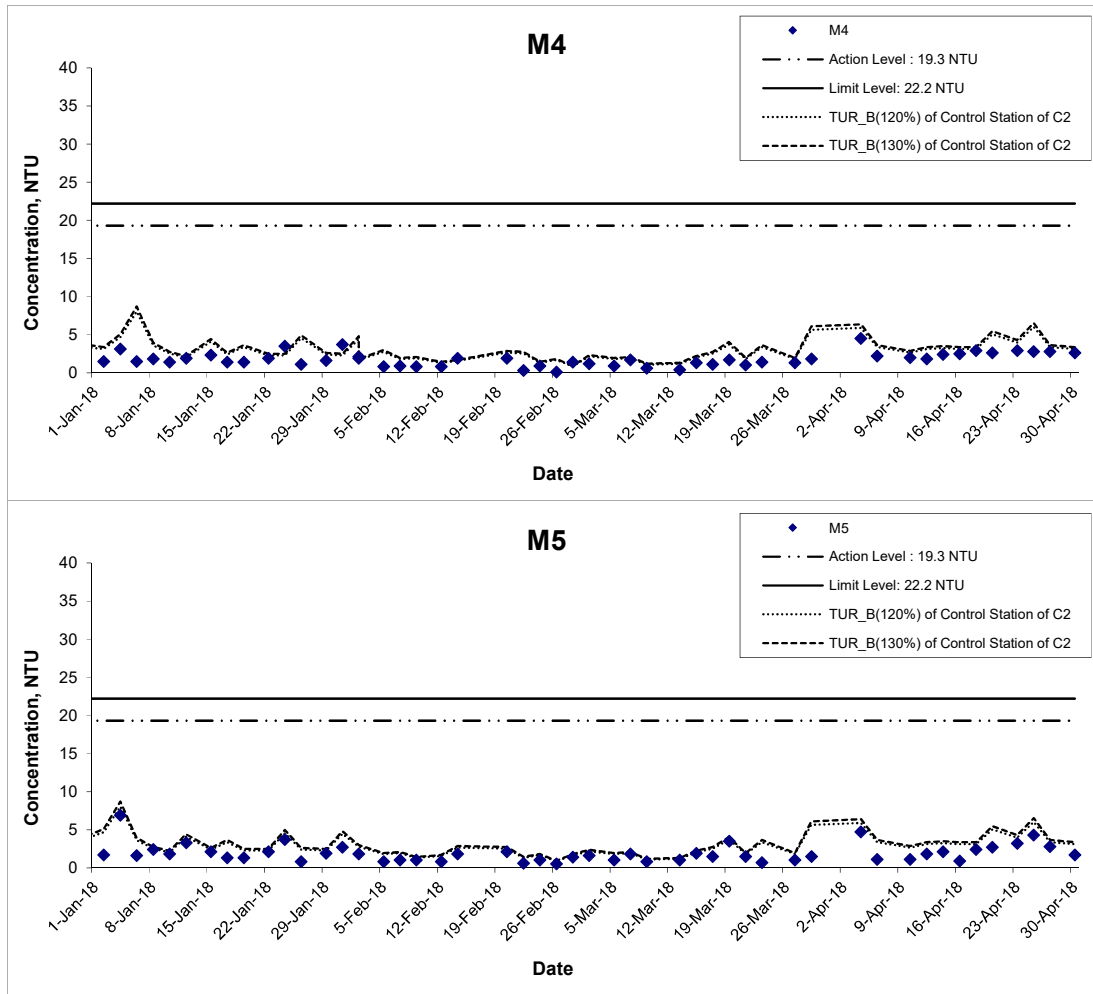

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S




Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Flood Tide

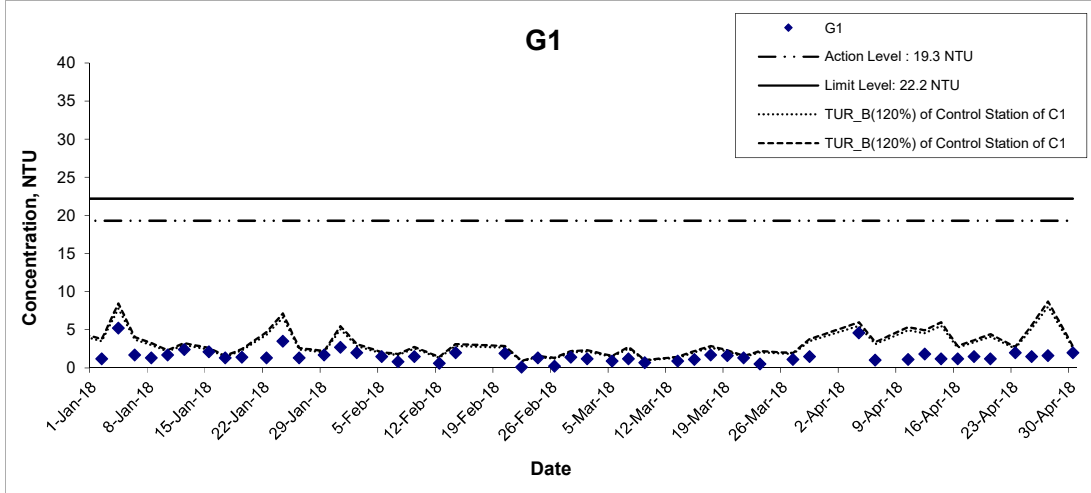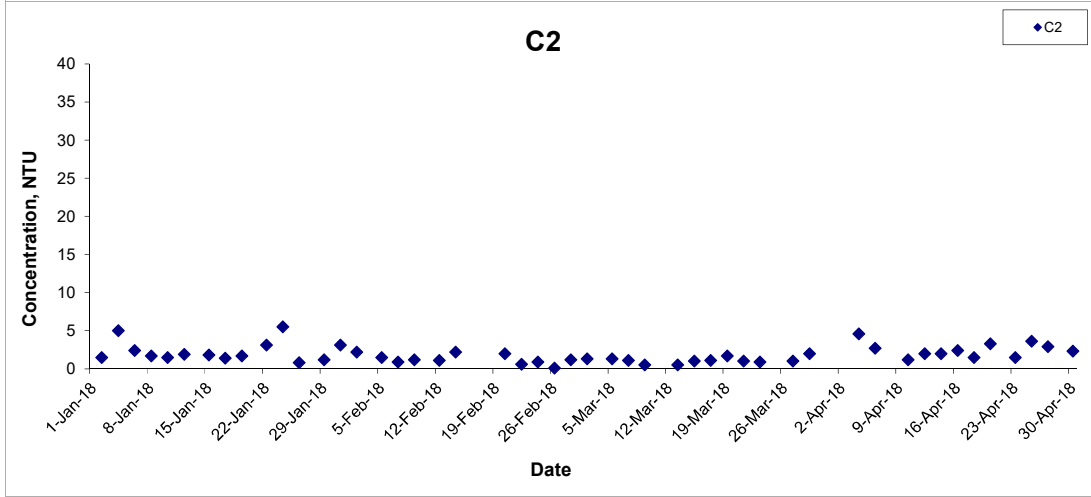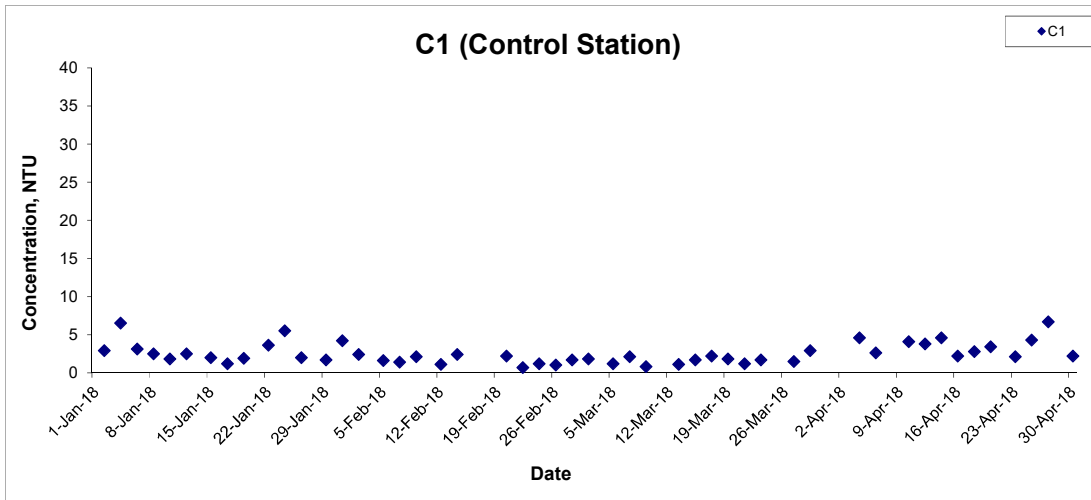

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S




Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Flood Tide

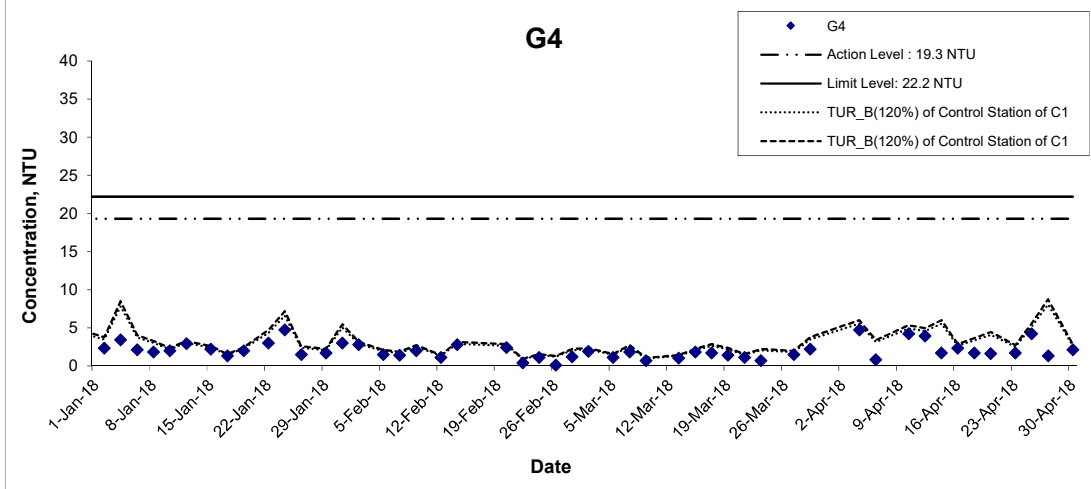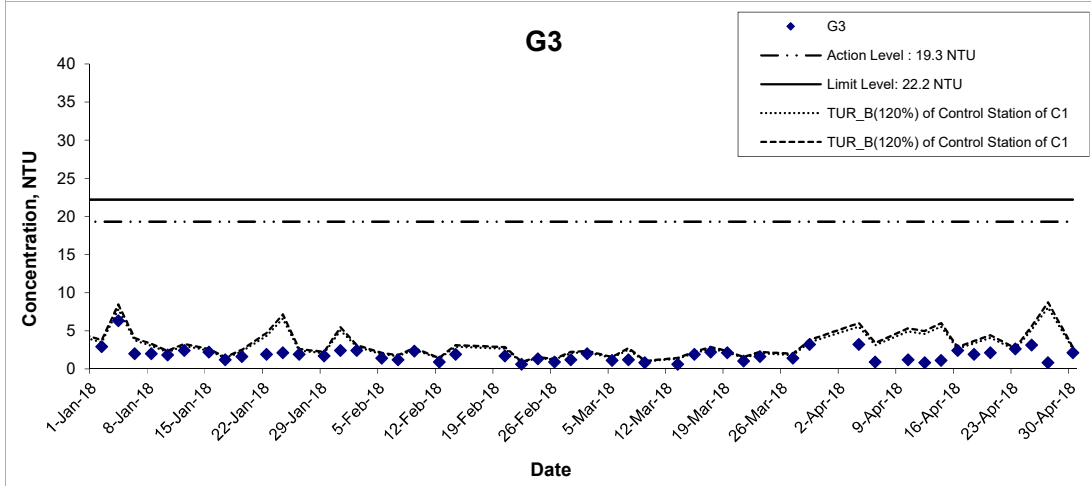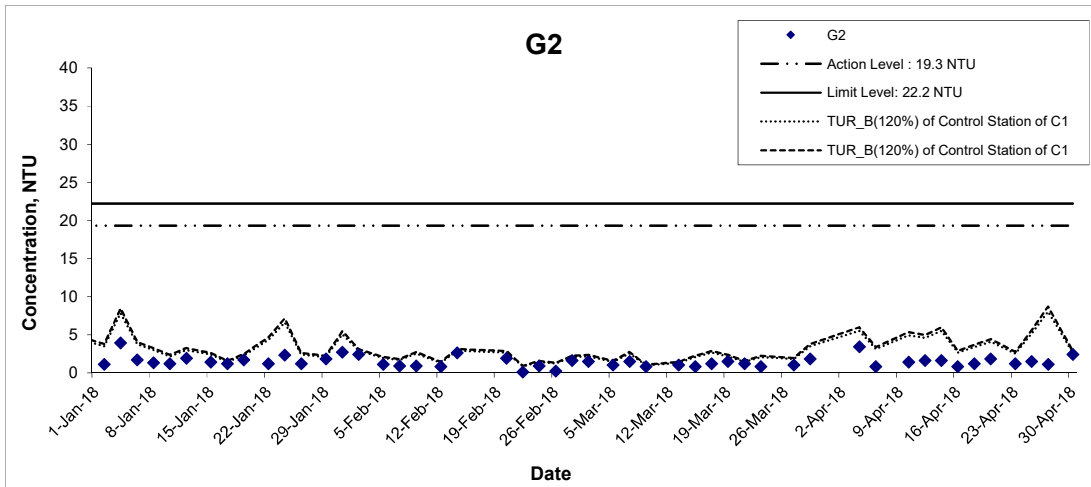

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Flood Tide

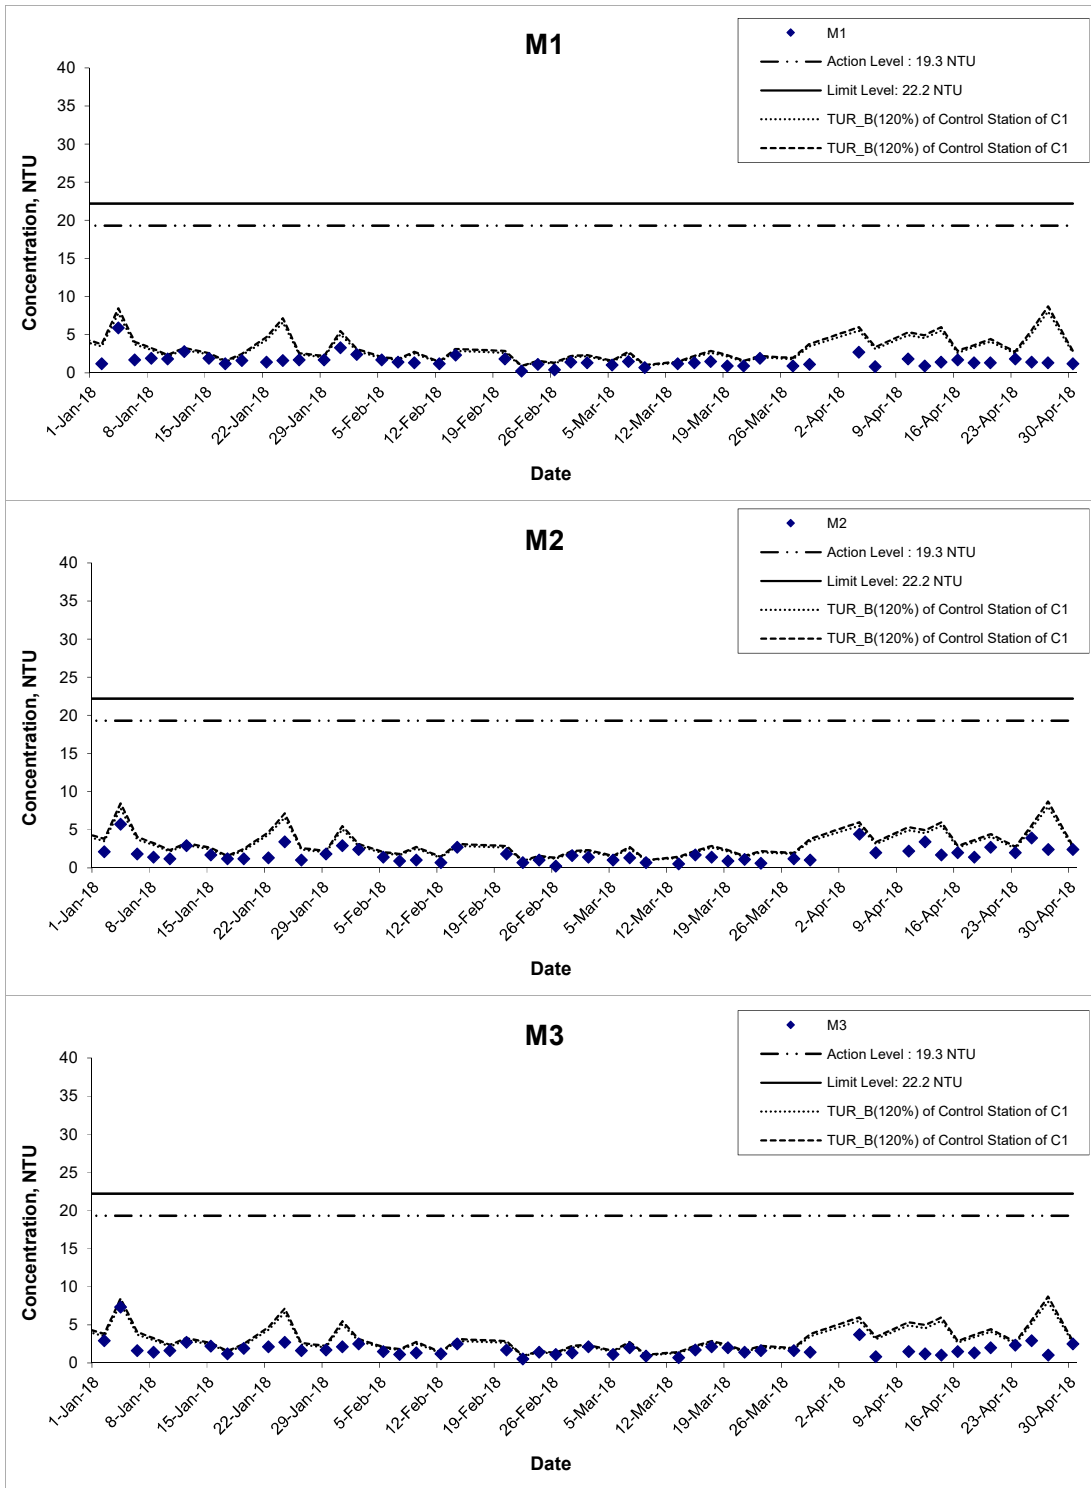

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Bottom) at Mid-Flood Tide

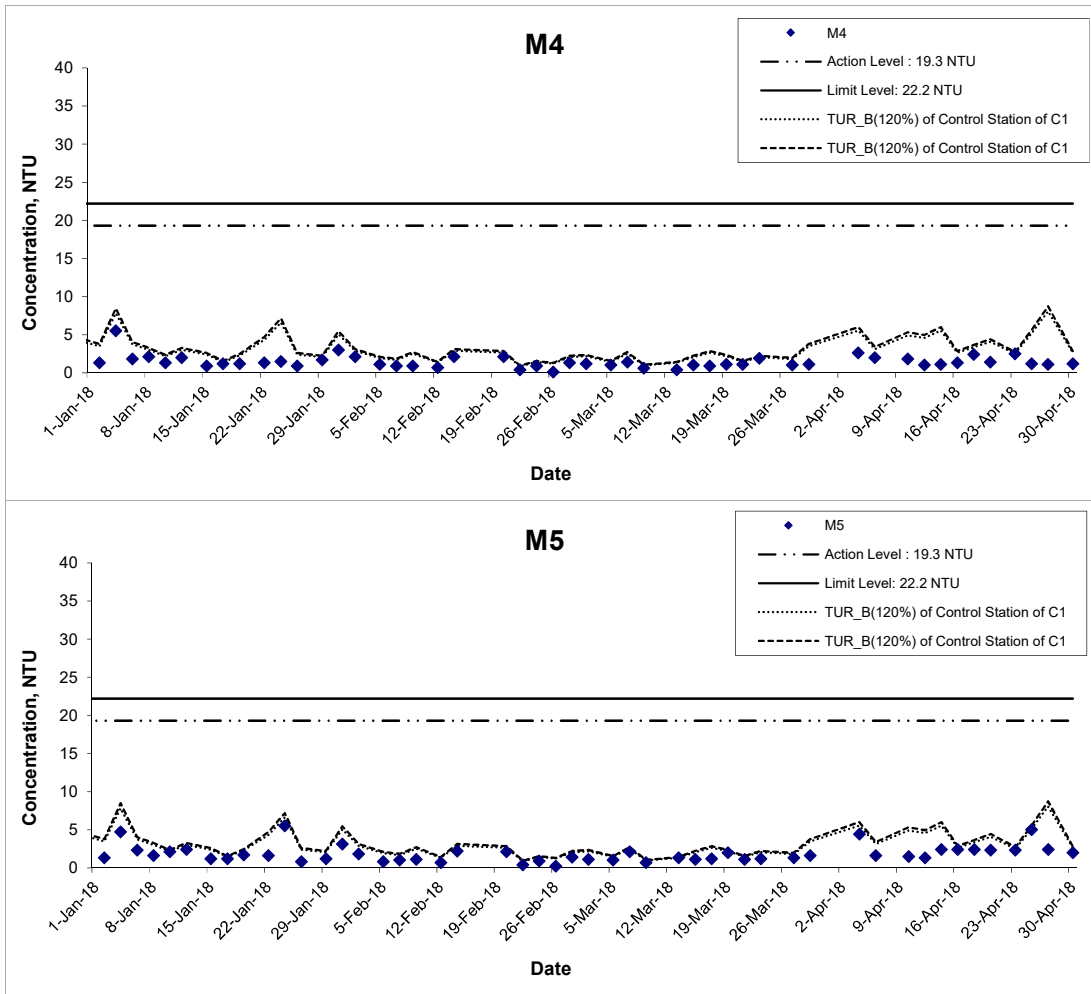

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Intake Level of WSD Salt Water Intake) at Mid-Ebb Tide

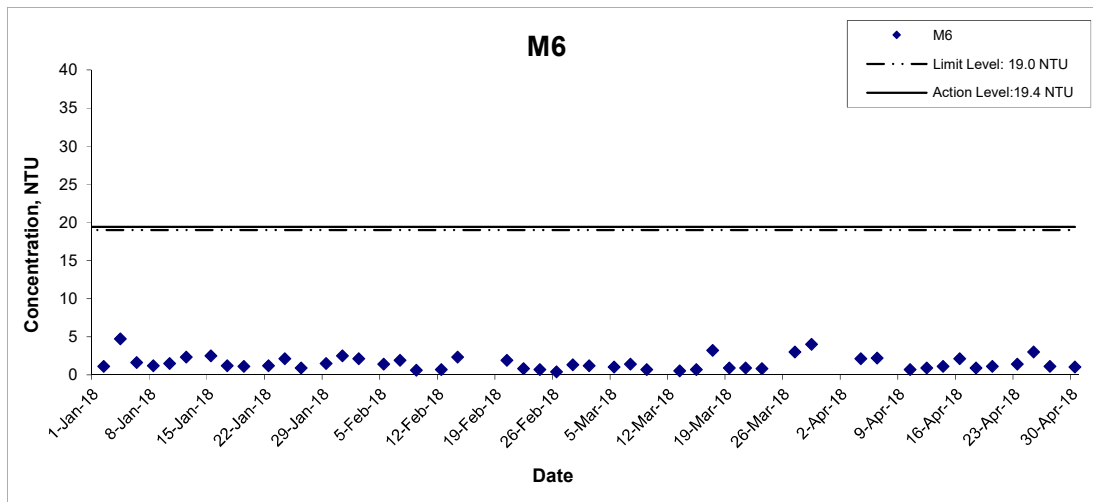

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Turbidity (Intake Level of WSD Salt Water Intake) at Mid-Flood Tide

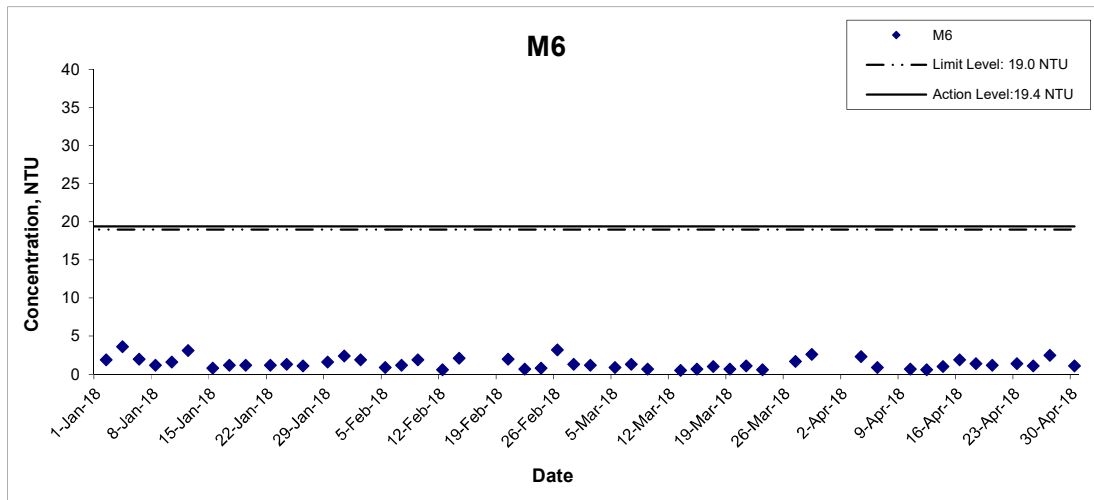

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Depth-averaged) at Mid-Ebb Tide

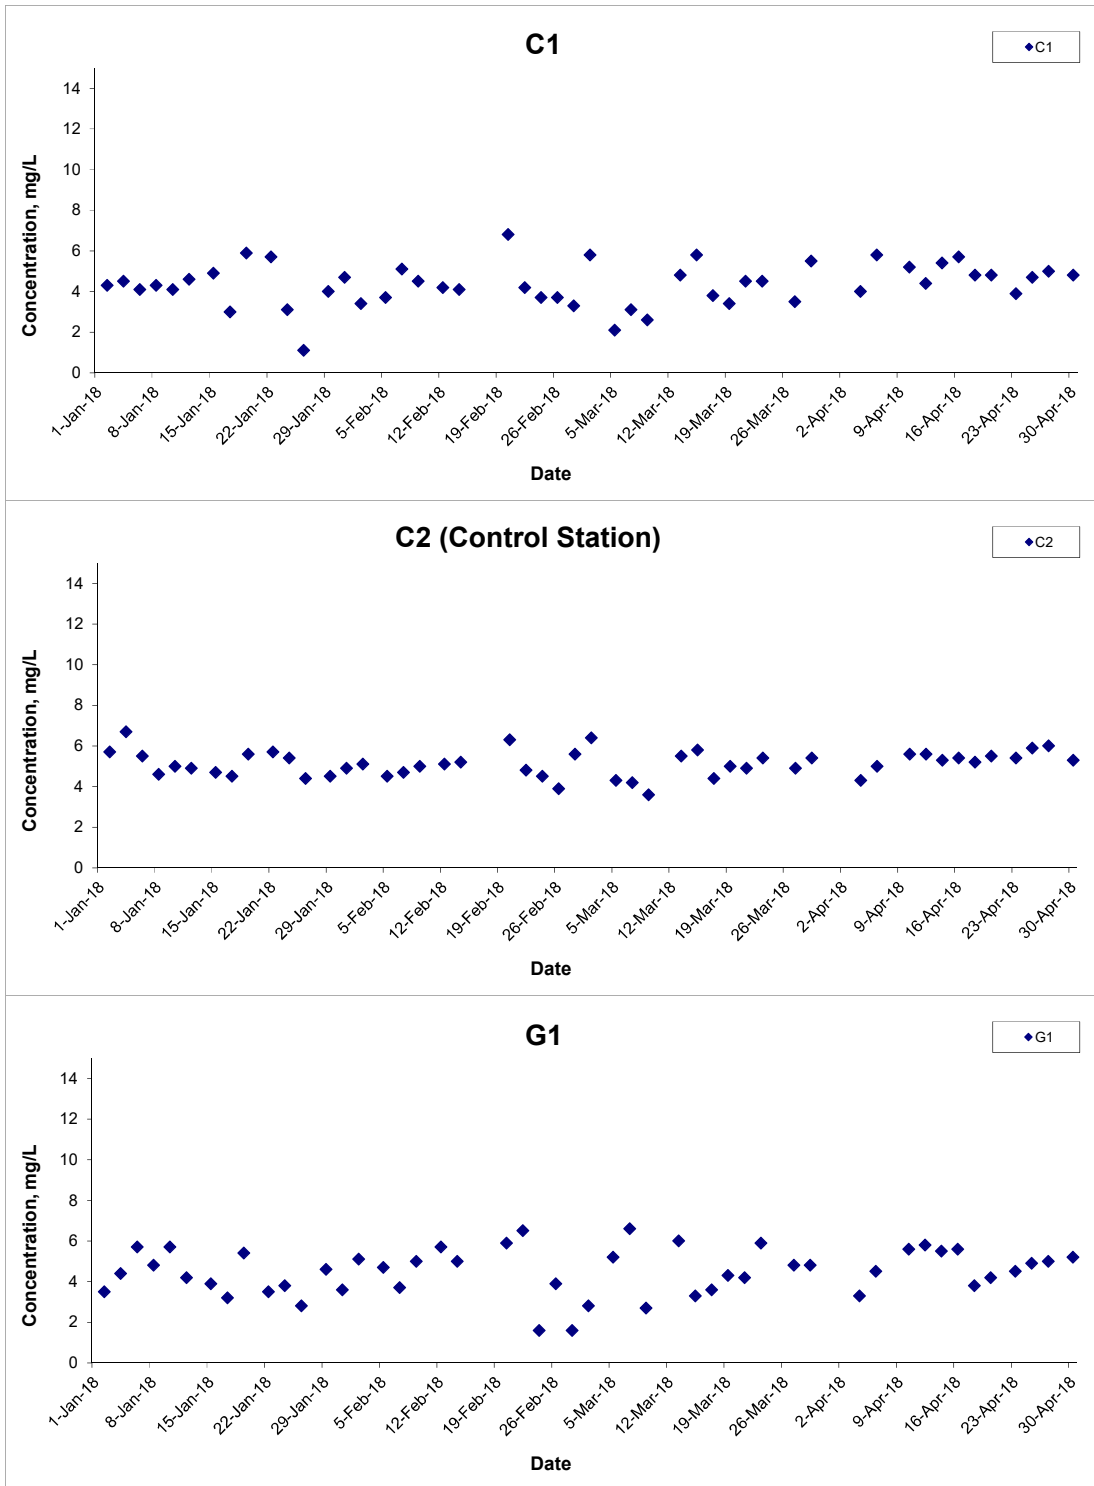


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S
Date Apr 18

Project No. MA16034
Appendix I



Suspended Solids (Depth-averaged) at Mid-Ebb Tide

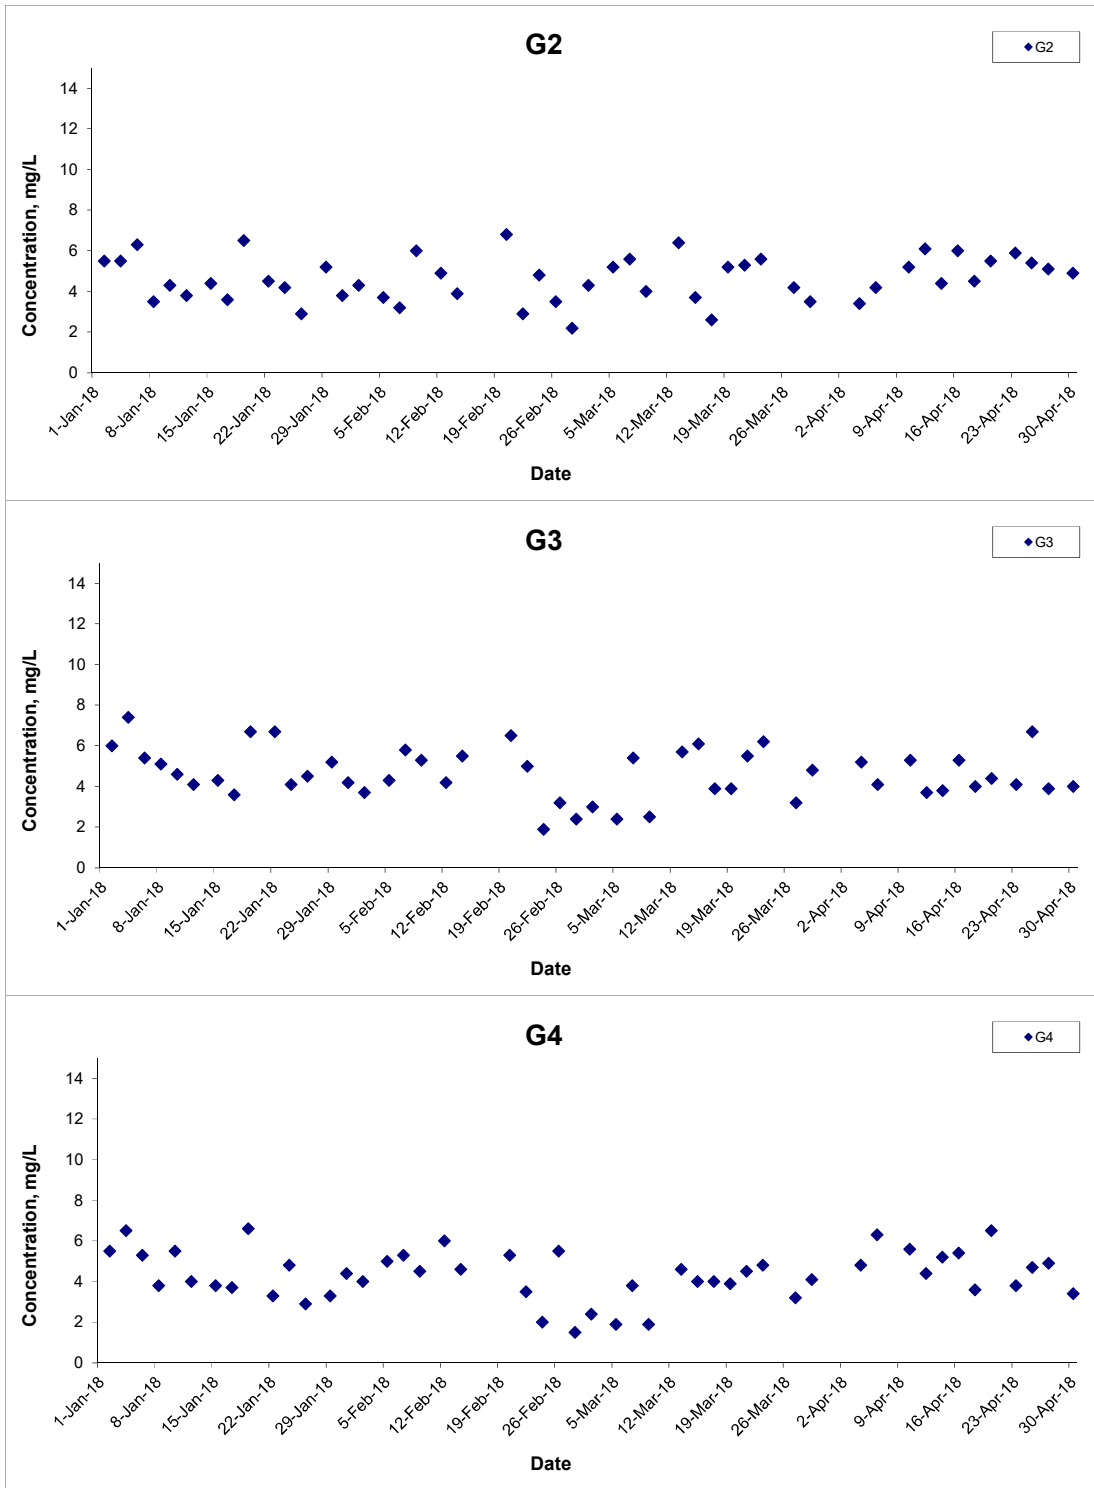


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S
Date Apr 18

Project No. MA16034
Appendix I



Suspended Solids (Depth-averaged) at Mid-Ebb Tide

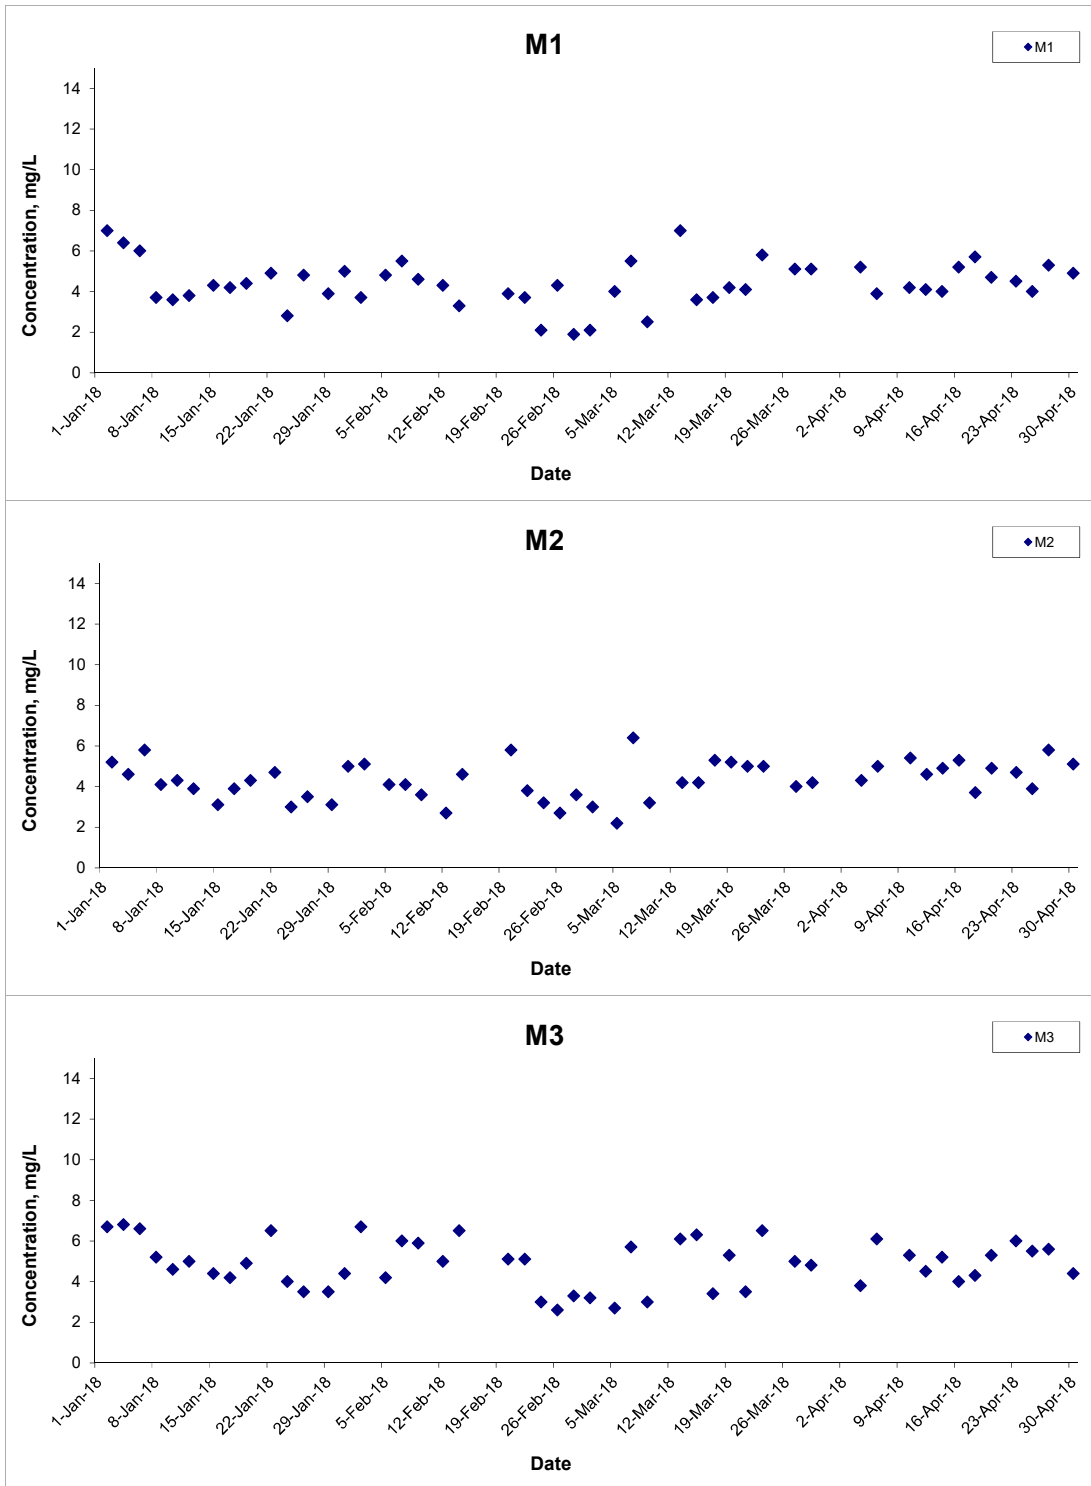

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Depth-averaged) at Mid-Ebb Tide

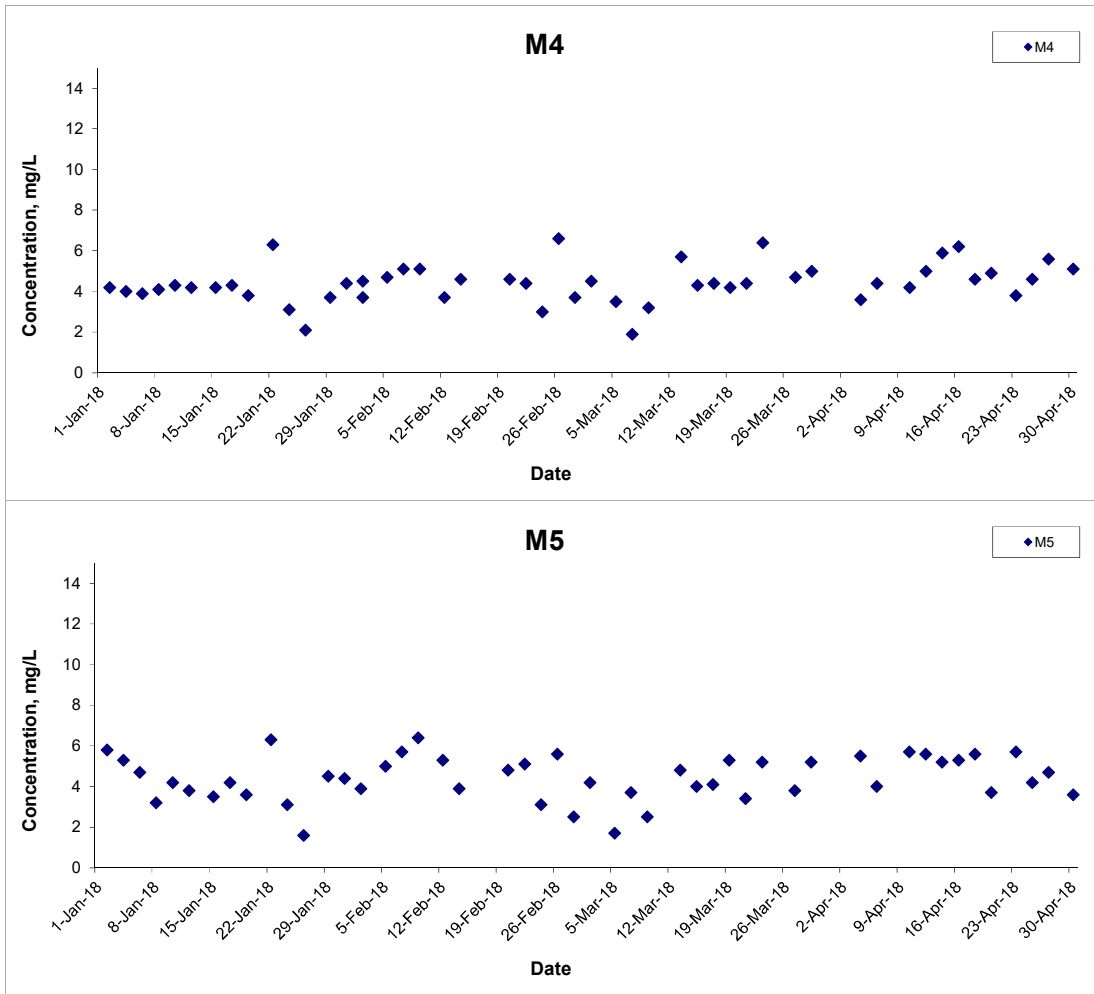

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Depth-averaged) at Mid-Flood Tide

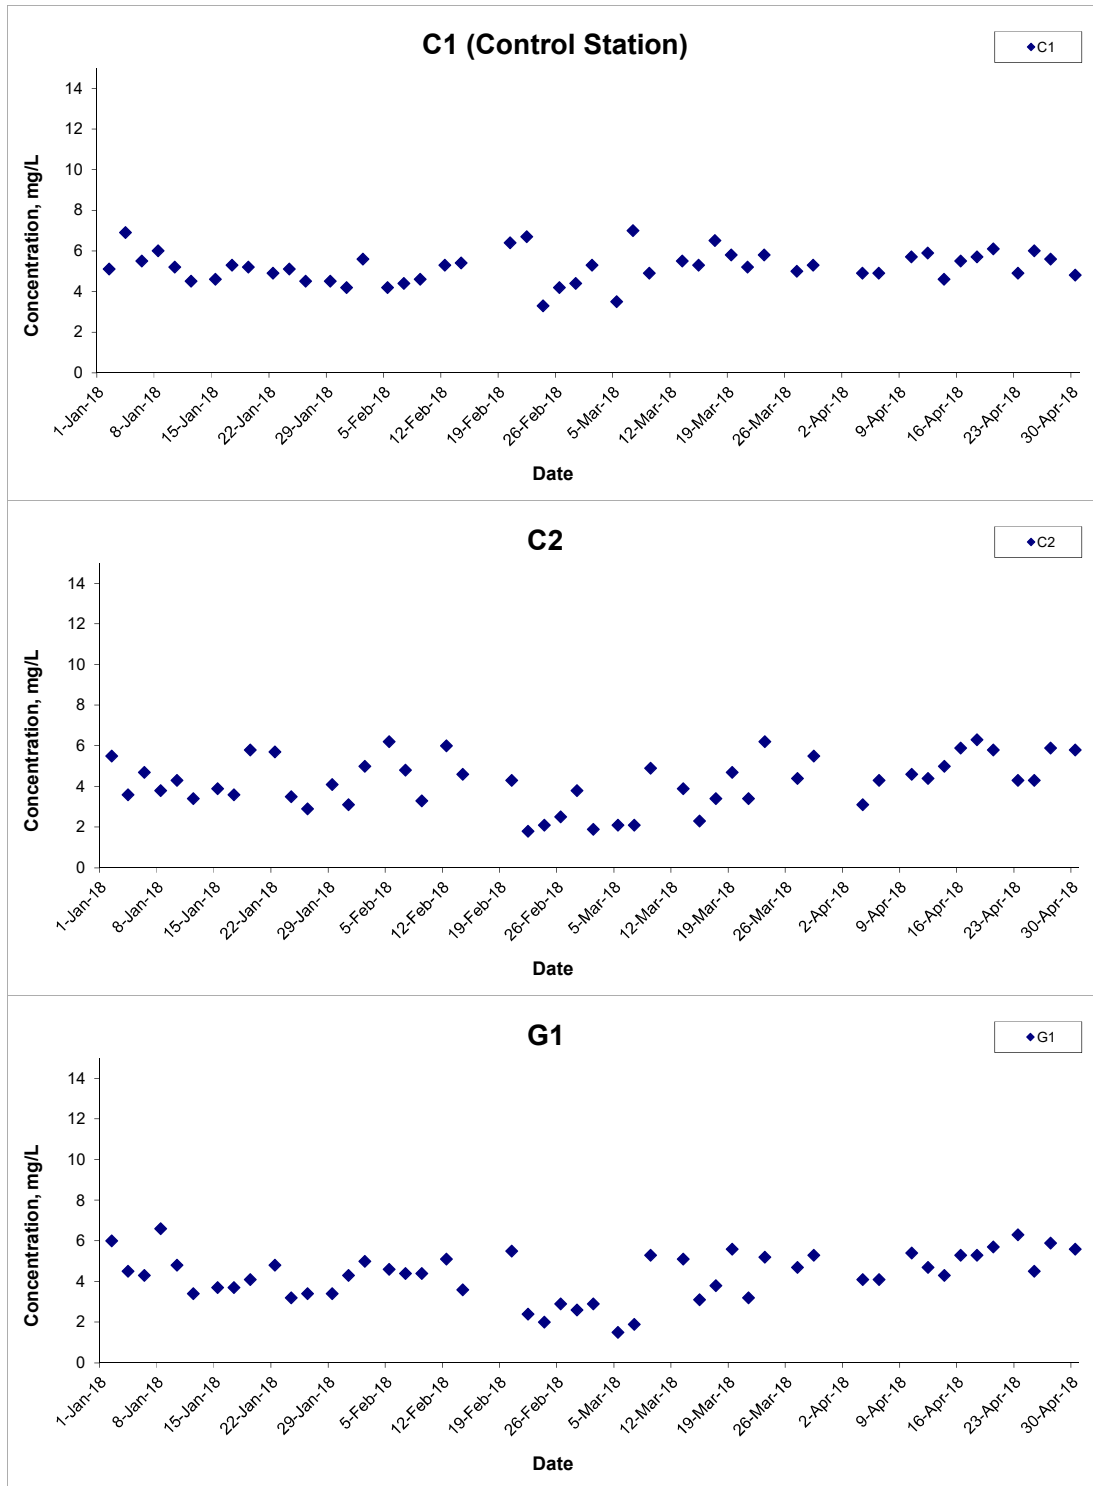

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Depth-averaged) at Mid-Flood Tide

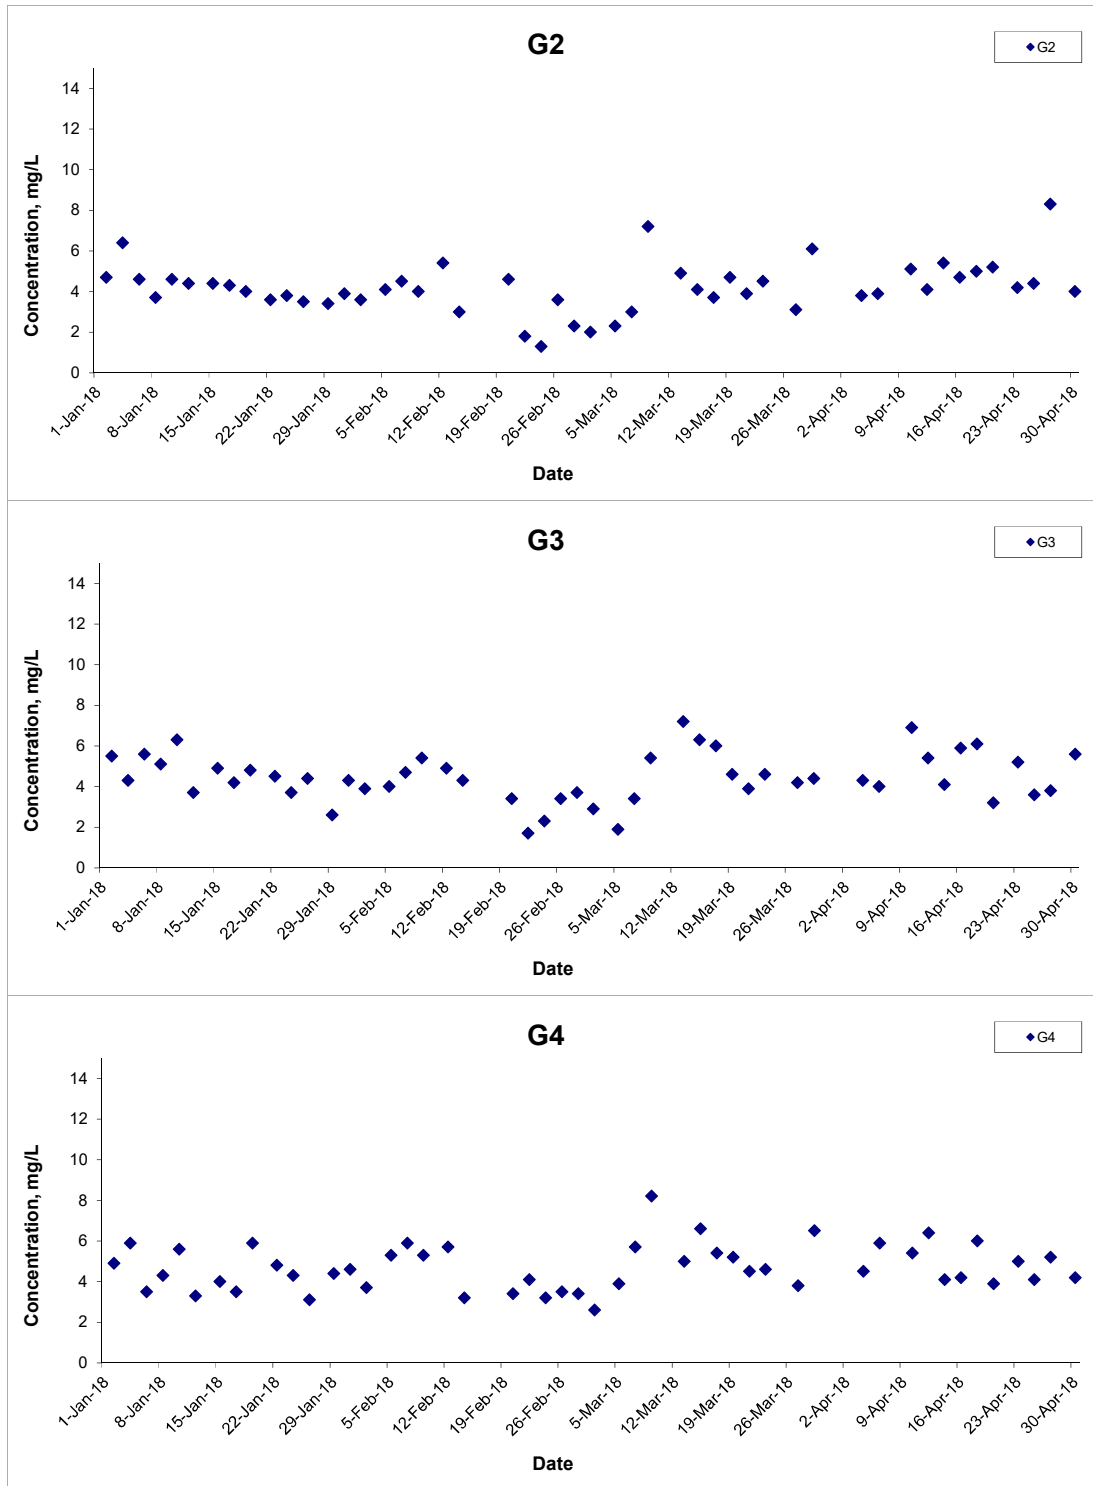


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S
Date Apr 18

Project No. MA16034
Appendix I



Suspended Solids (Depth-averaged) at Mid-Flood Tide

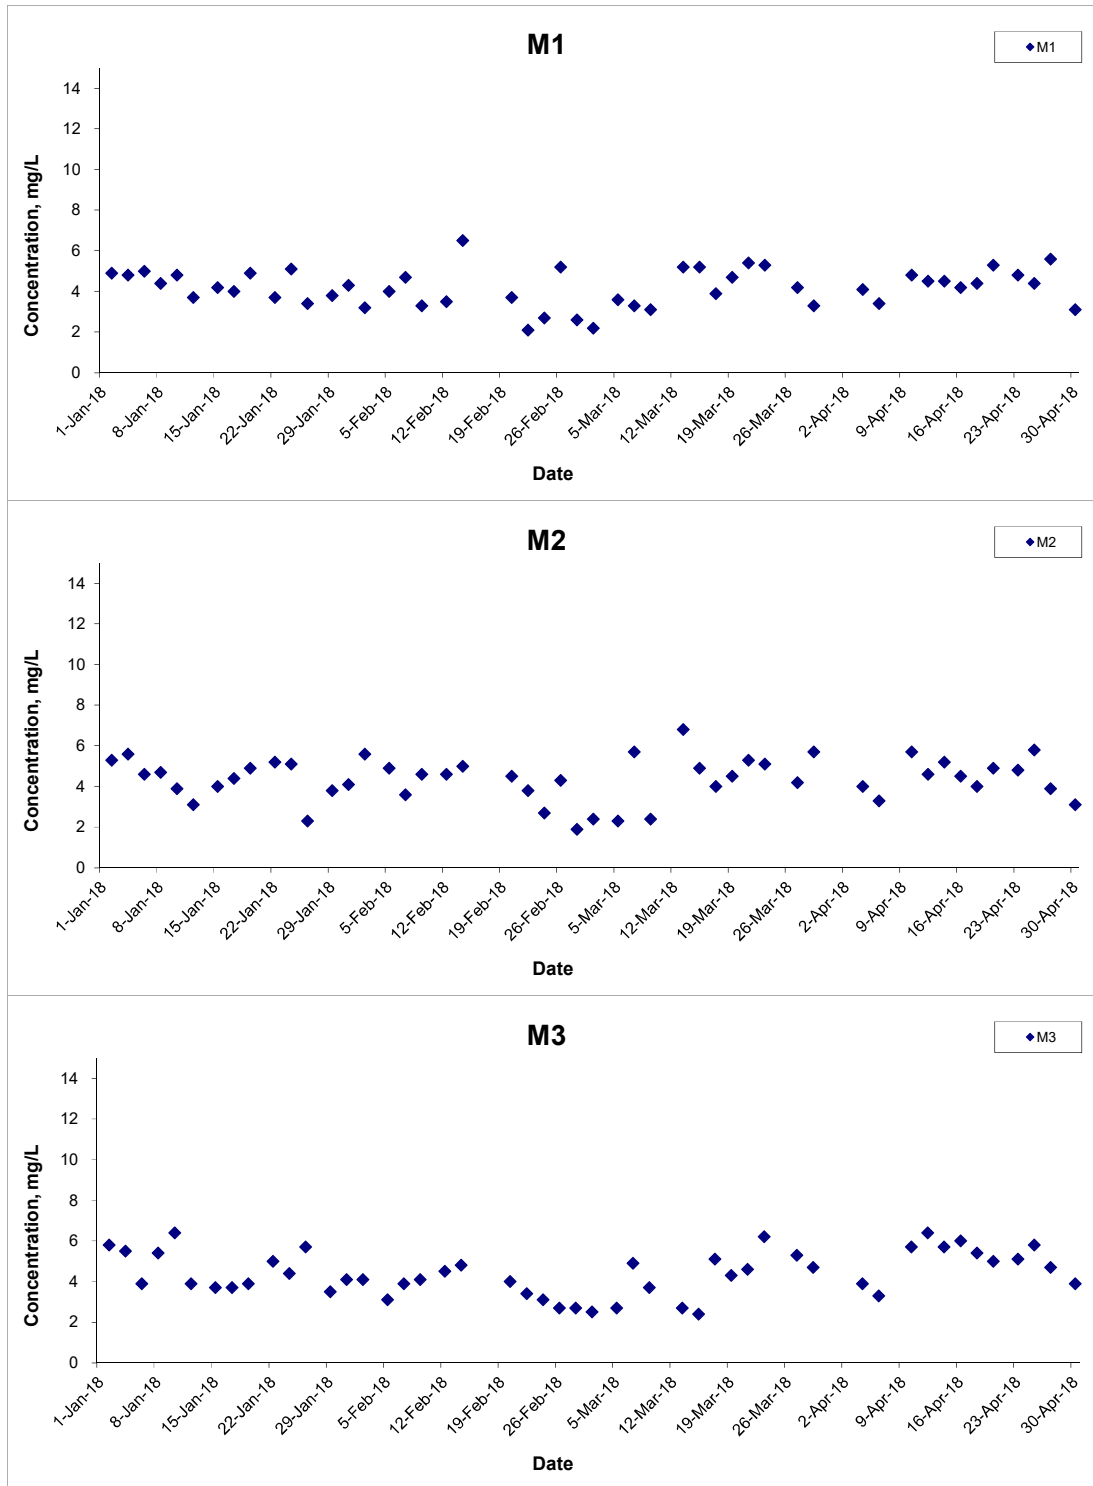

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Depth-averaged) at Mid-Flood Tide

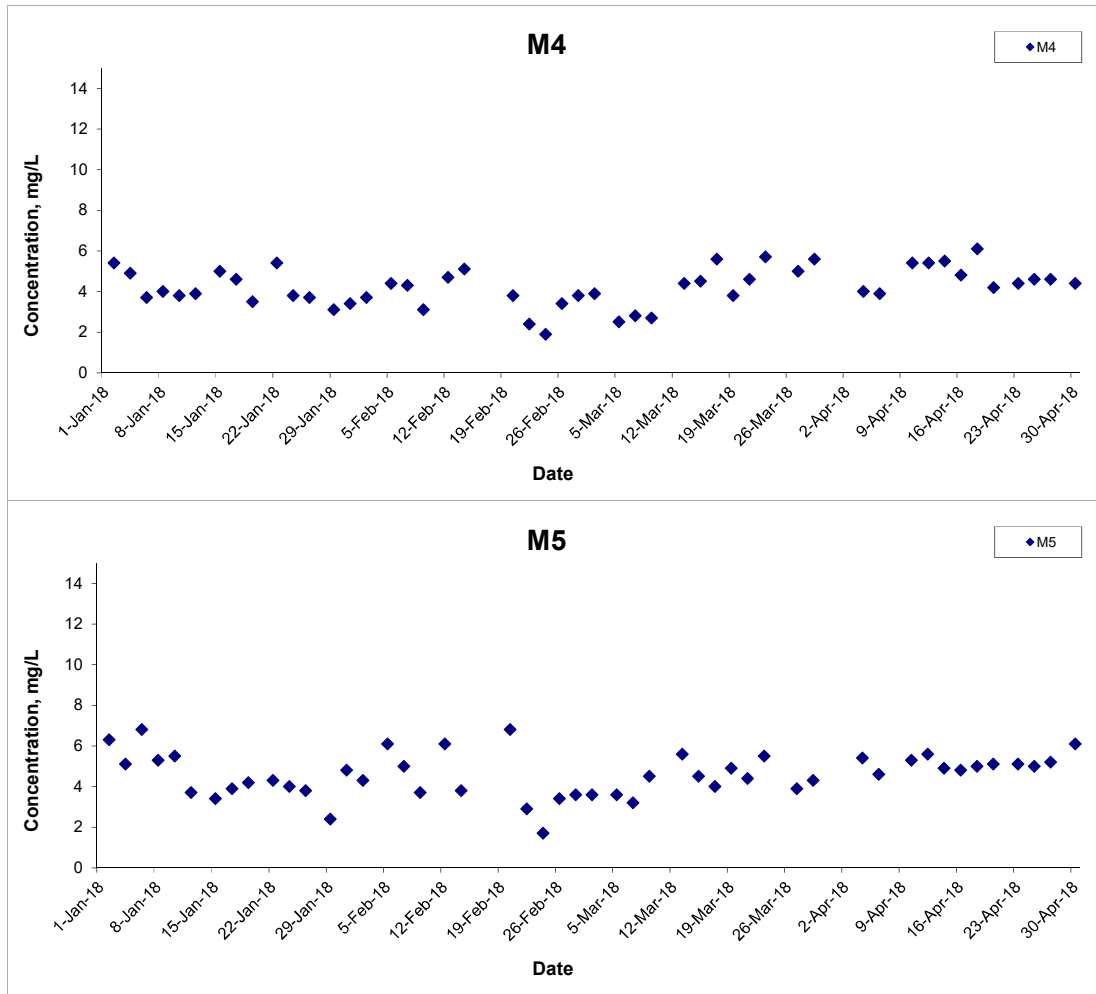

Title Agreement No. CE 59/2015(EP) Environmental Team for
Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring
Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Ebb Tide

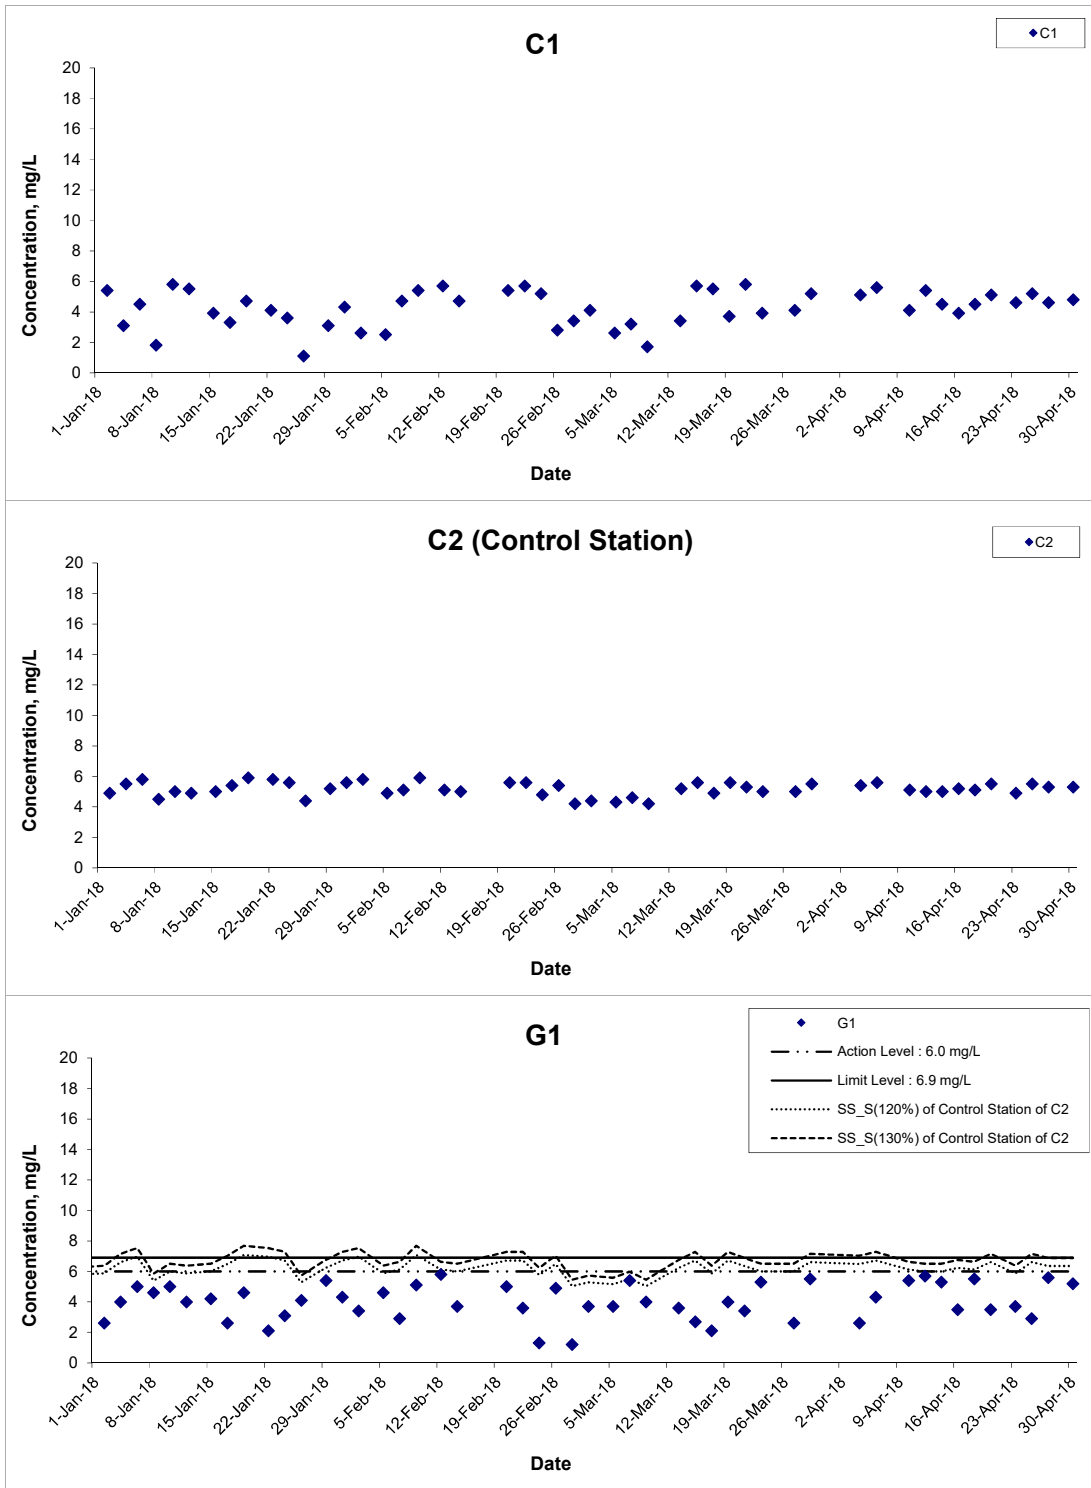

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Ebb Tide

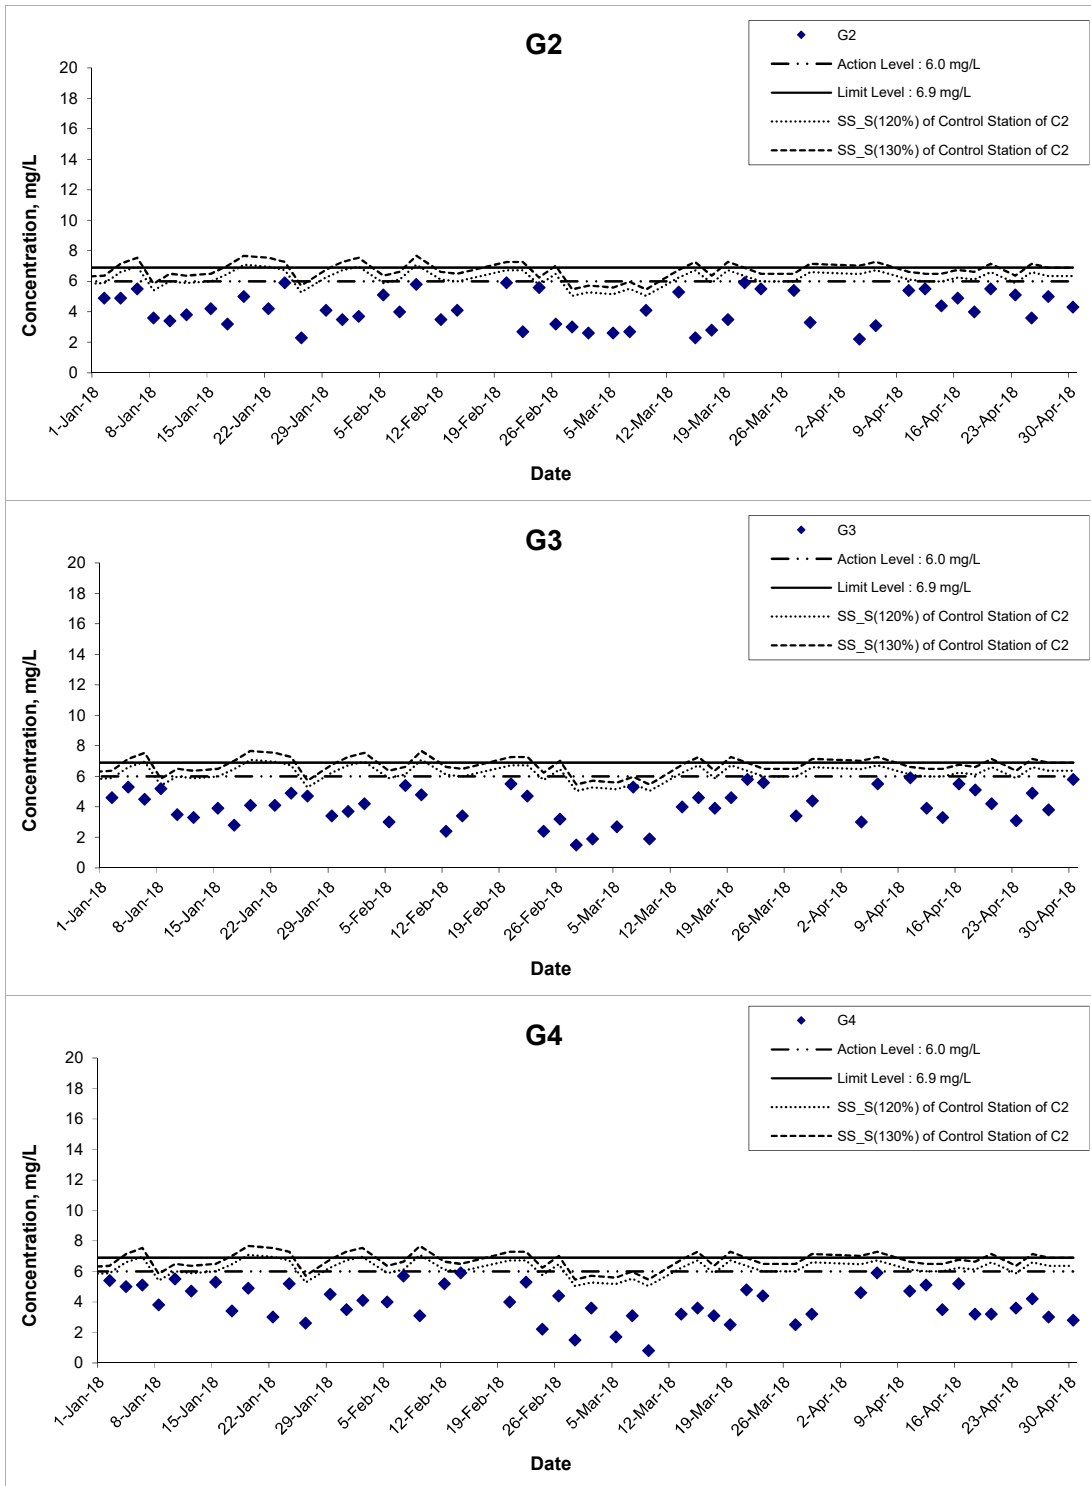

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Ebb Tide

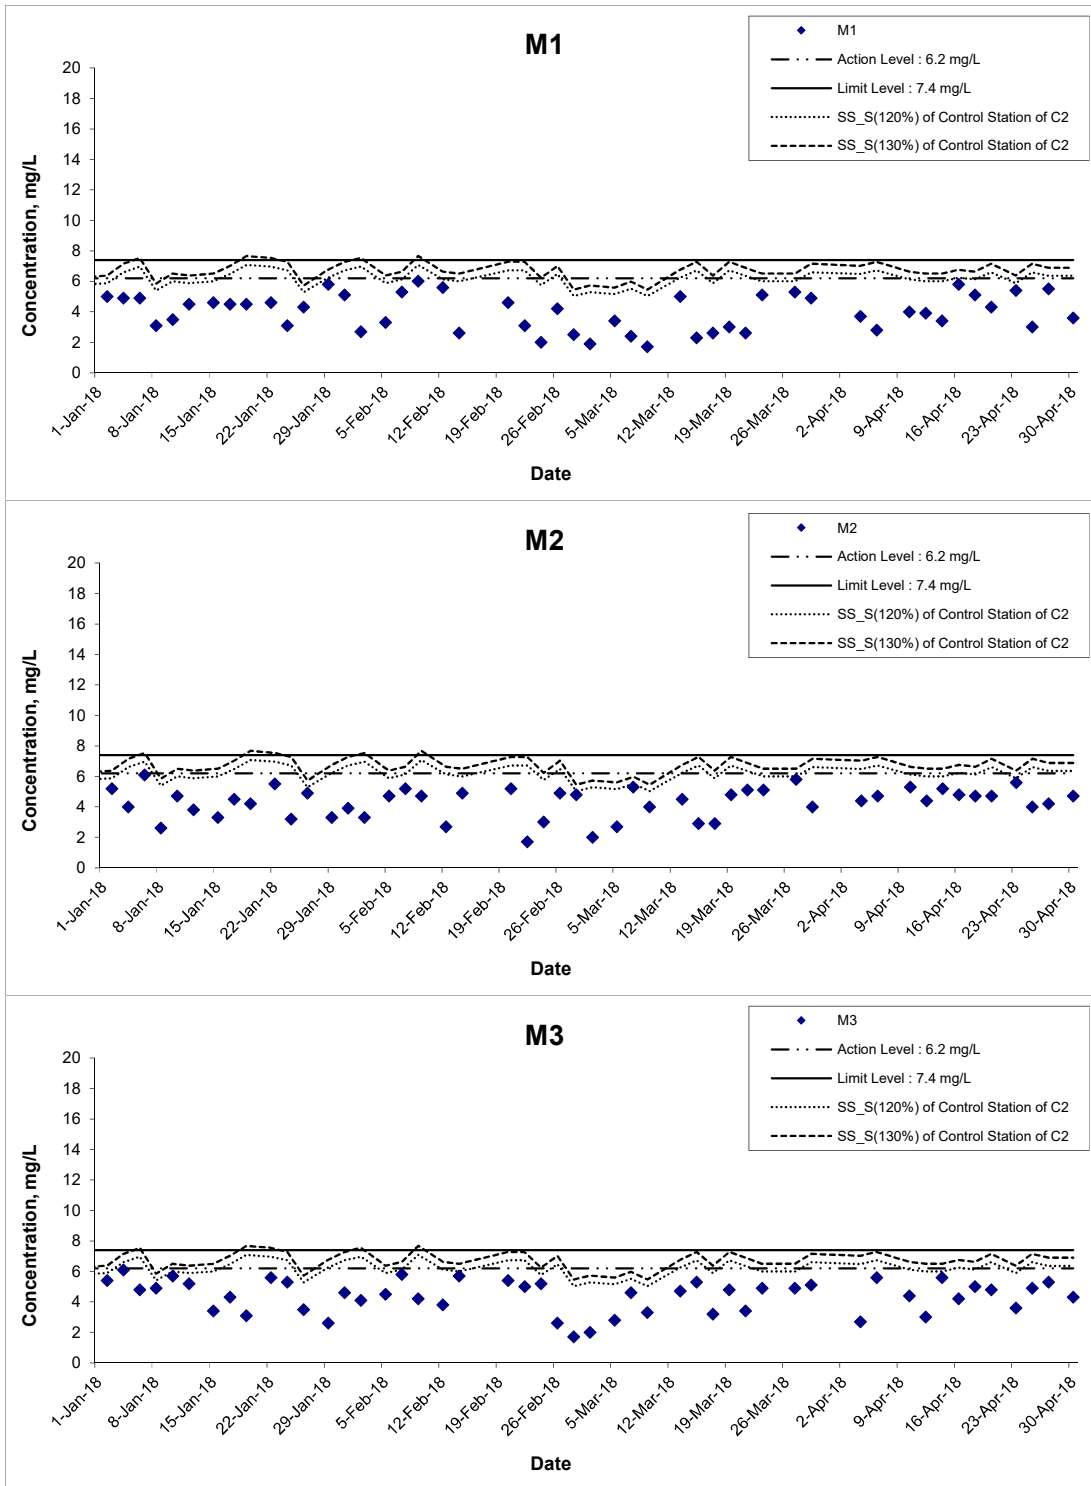


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S
Date Apr 18
Project No. MA16034
Appendix I



Suspended Solids (Surface) at Mid-Ebb Tide

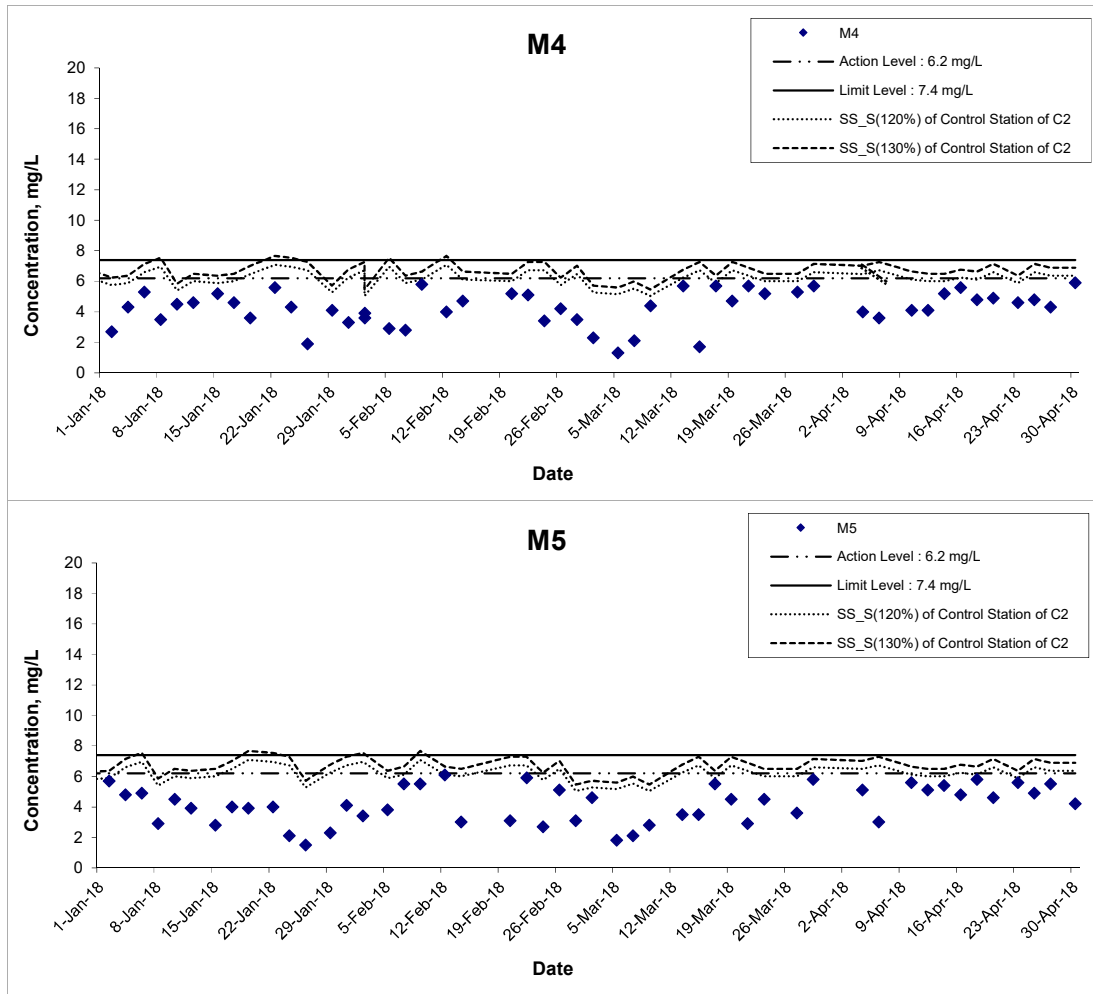

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Flood Tide

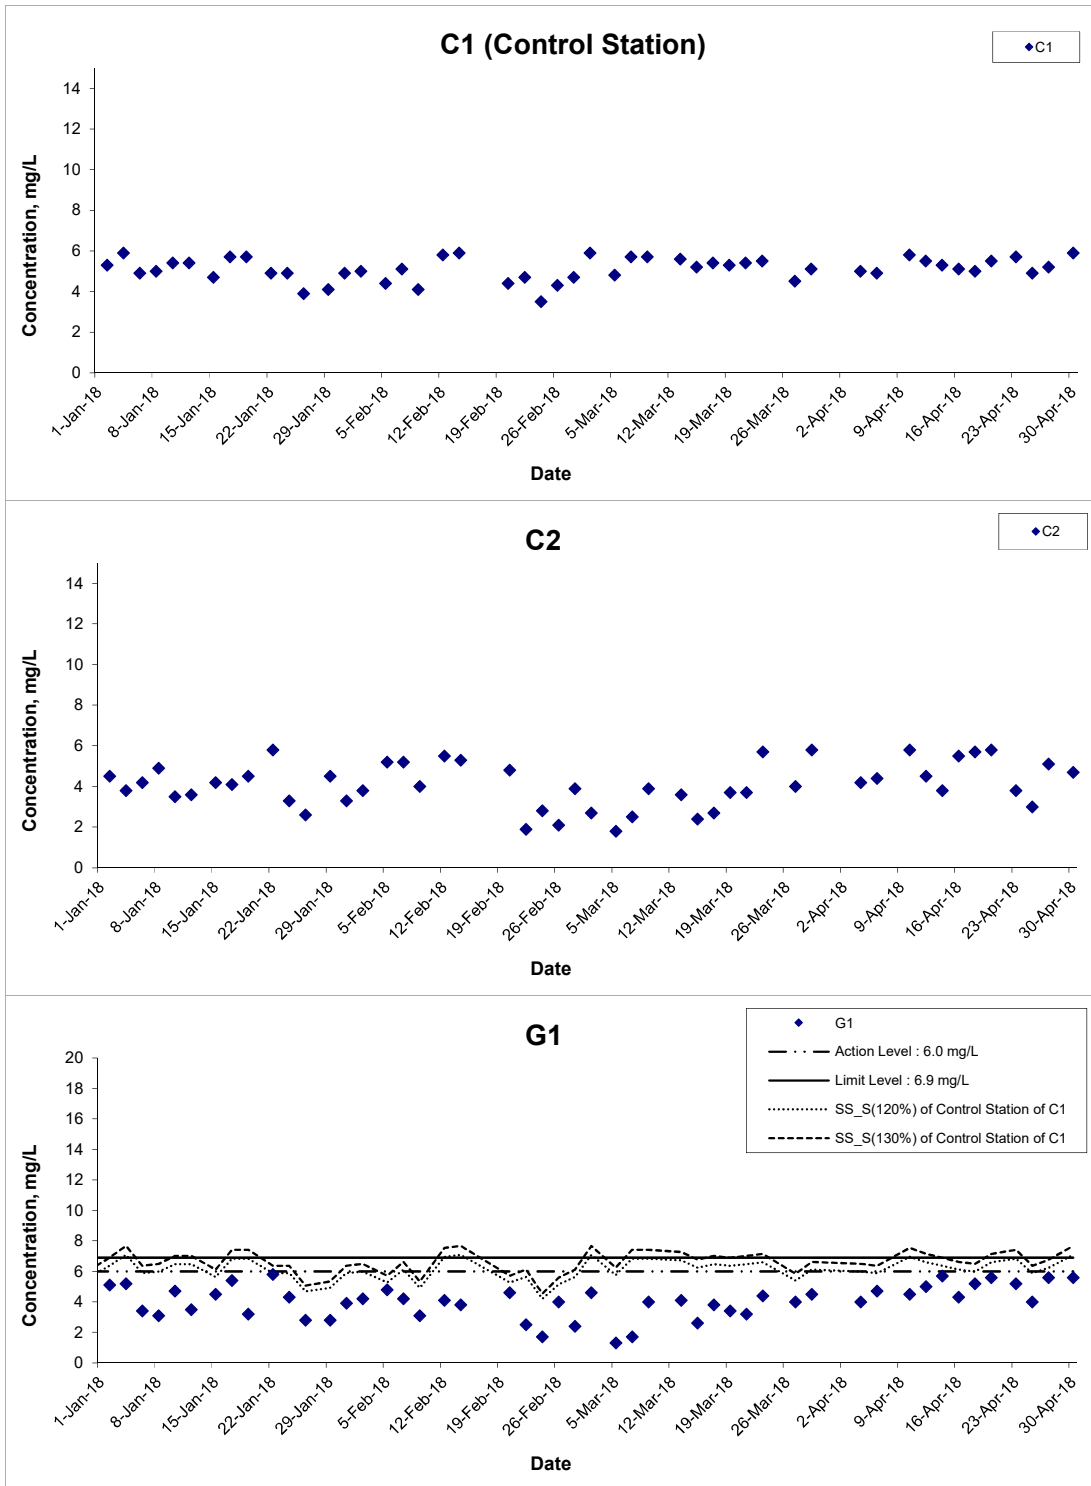

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Flood Tide

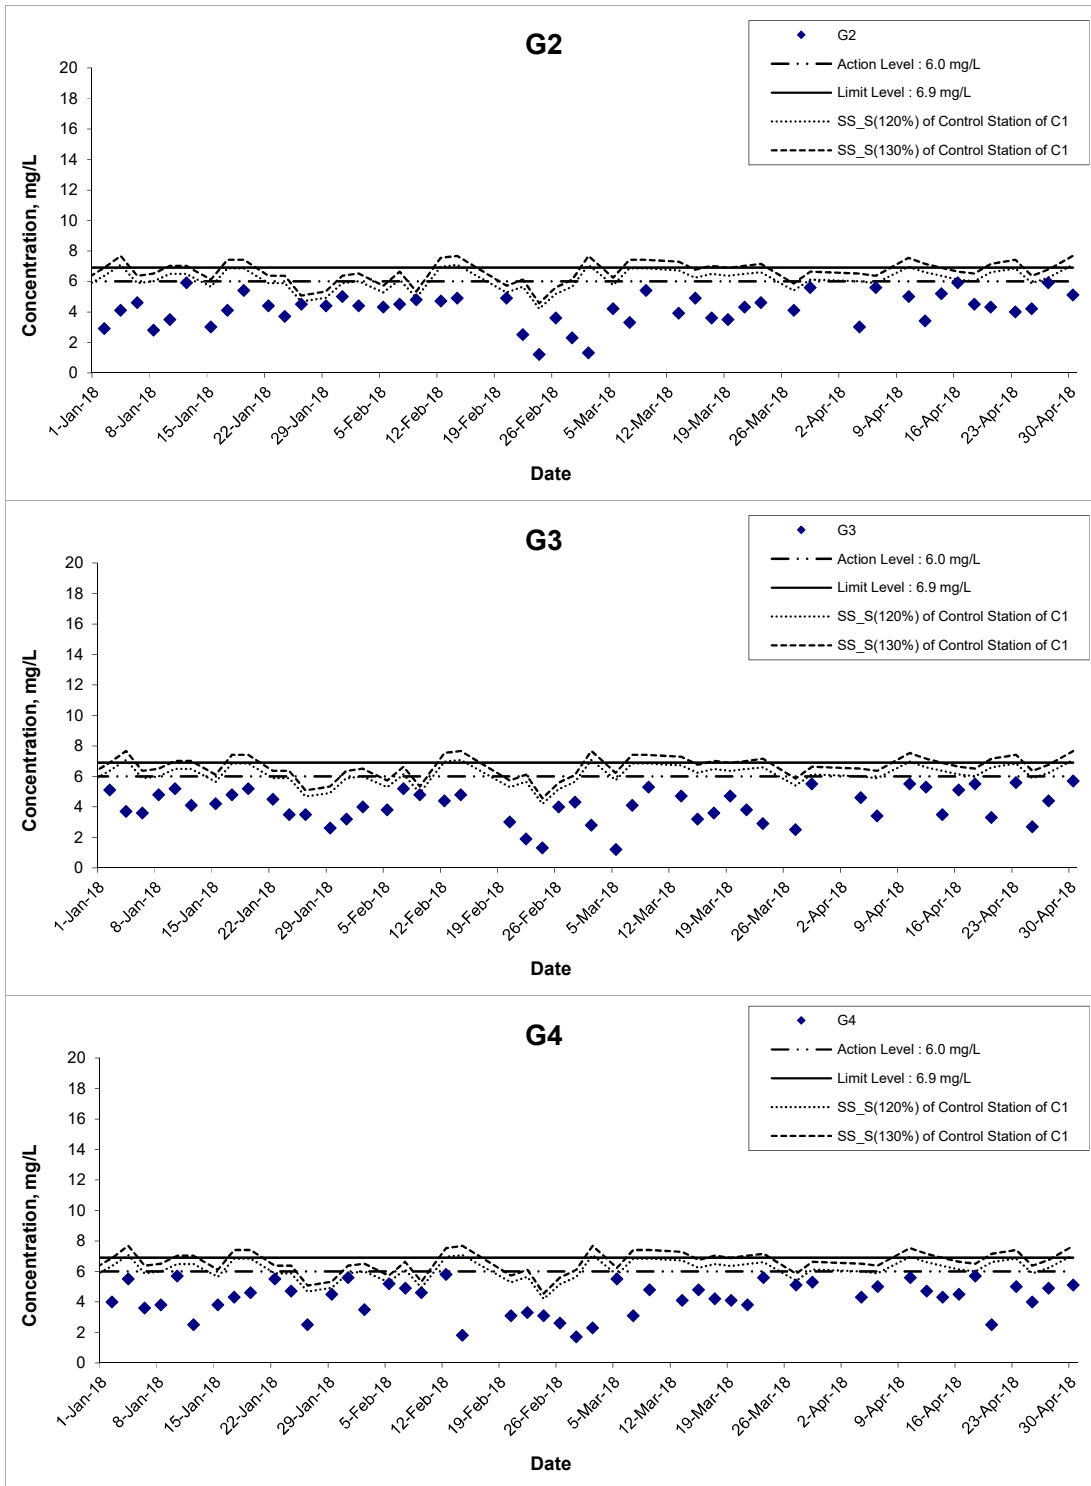

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Flood Tide

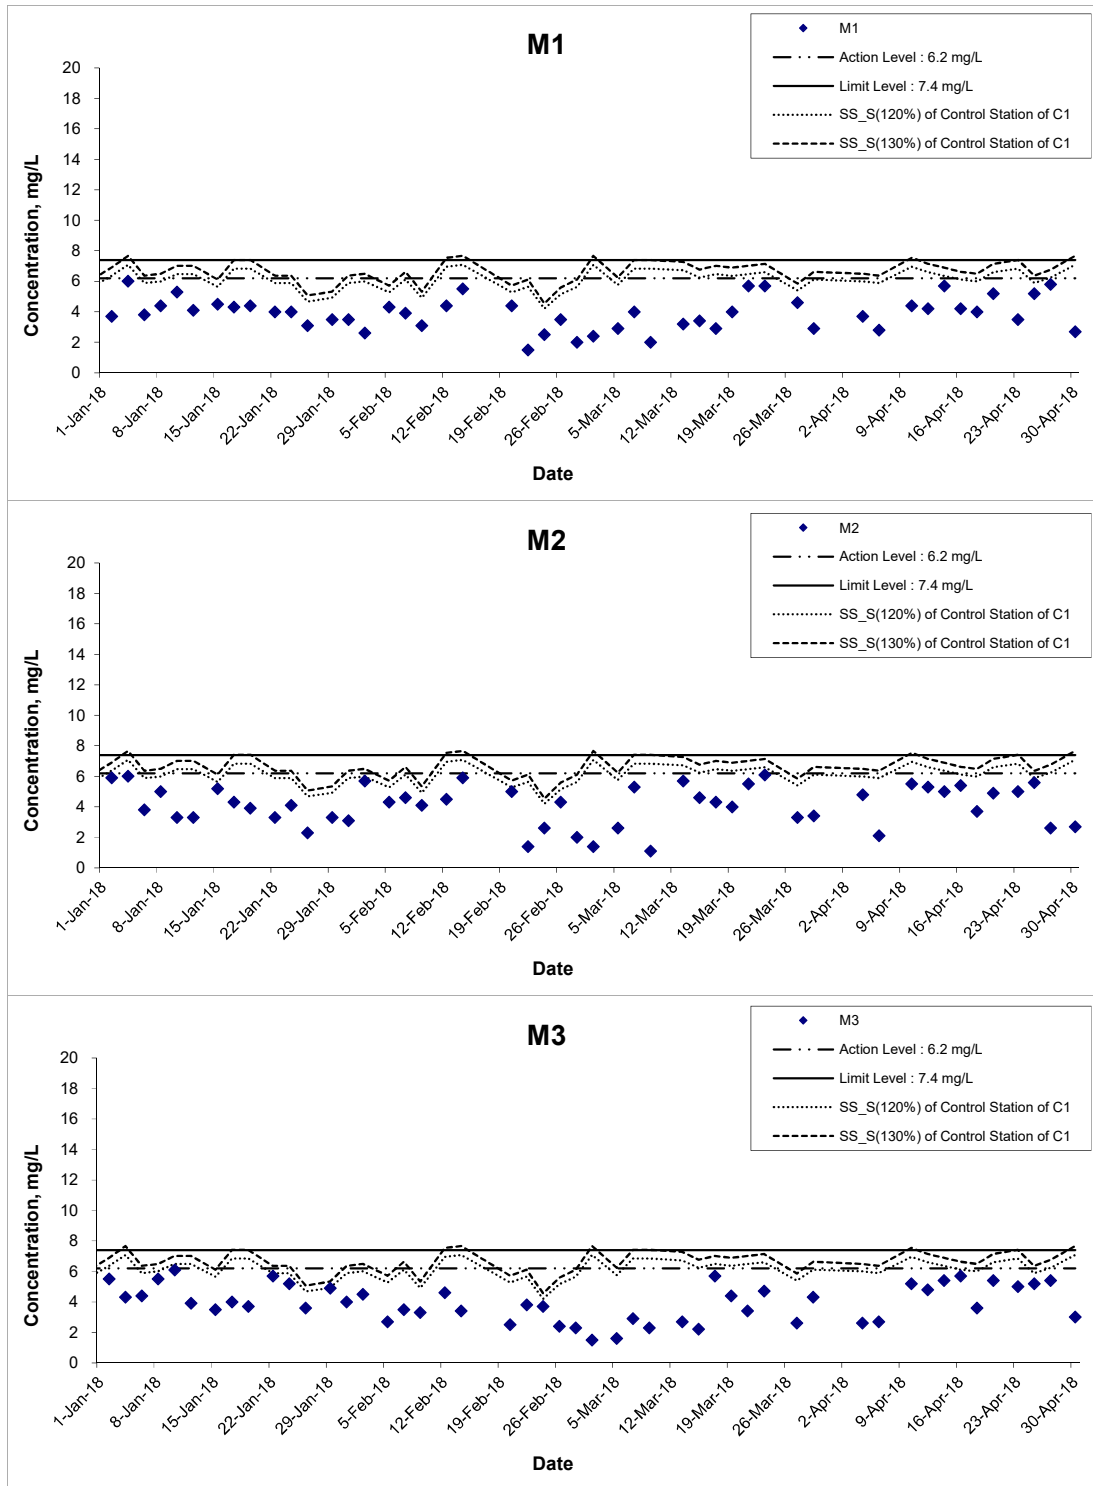

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Surface) at Mid-Flood Tide

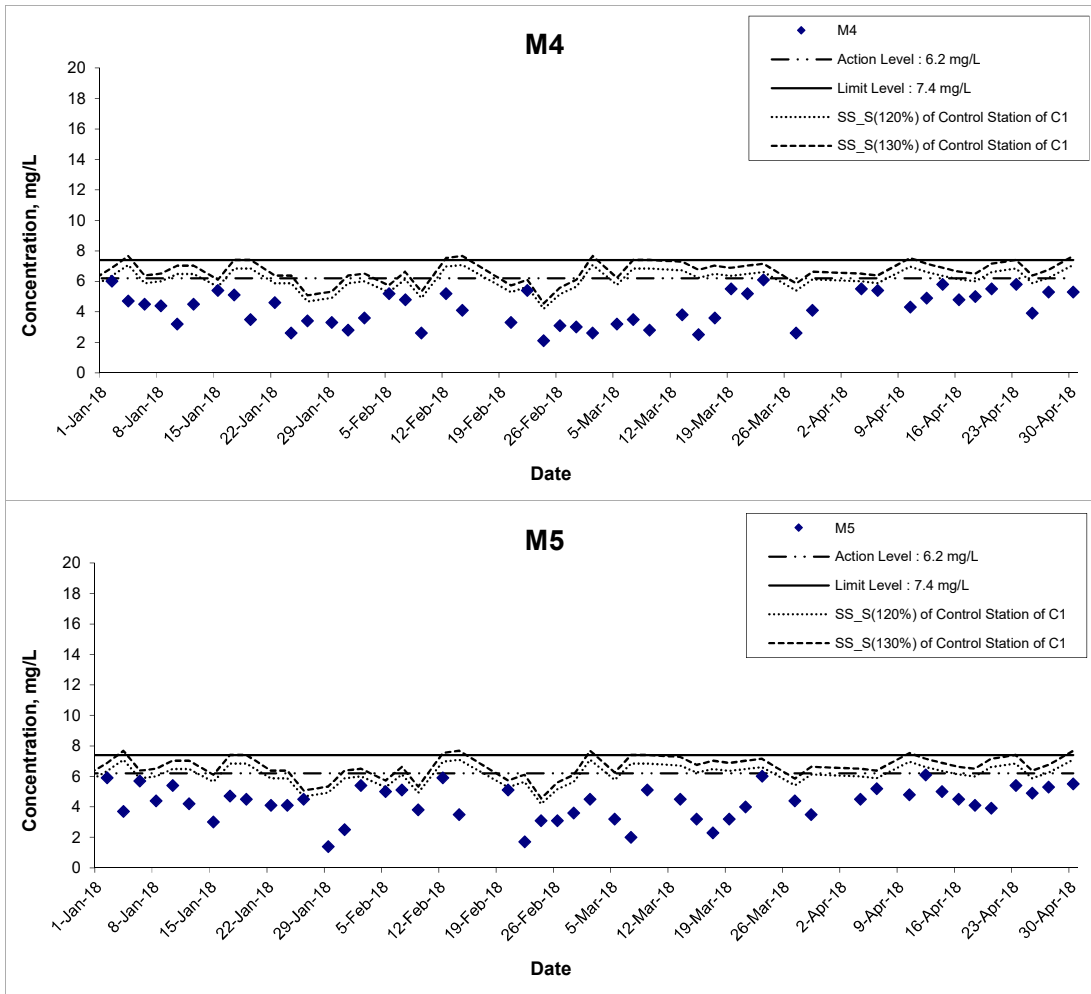

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Ebb Tide

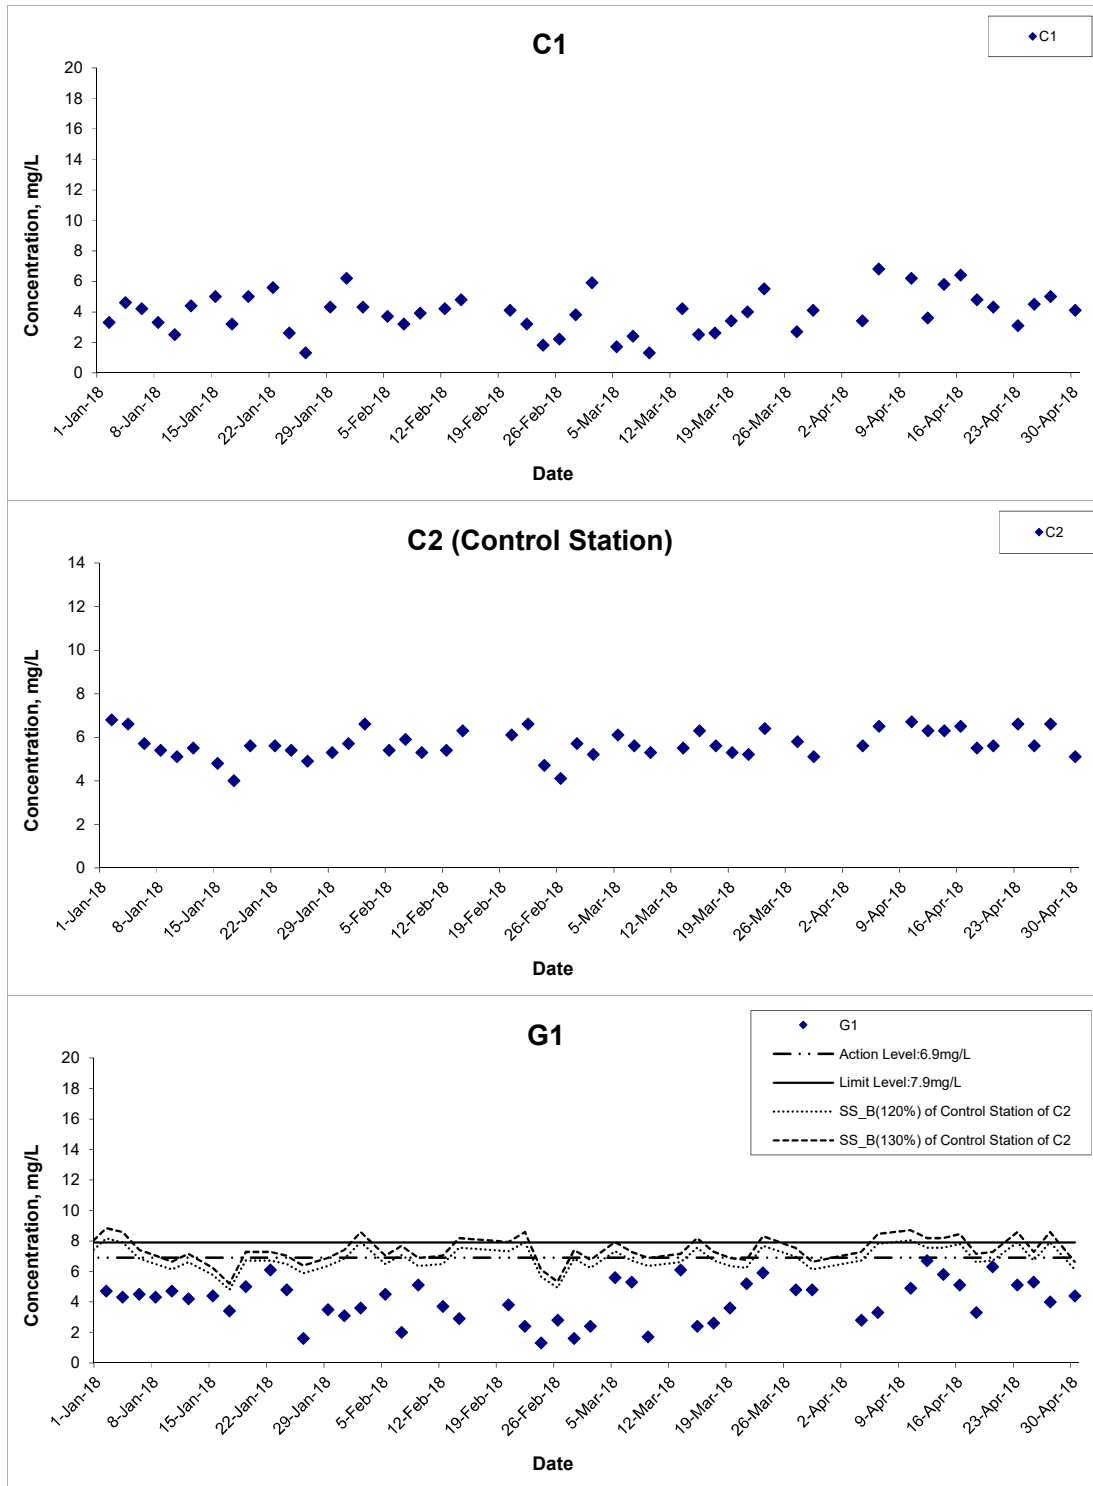

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Ebb Tide

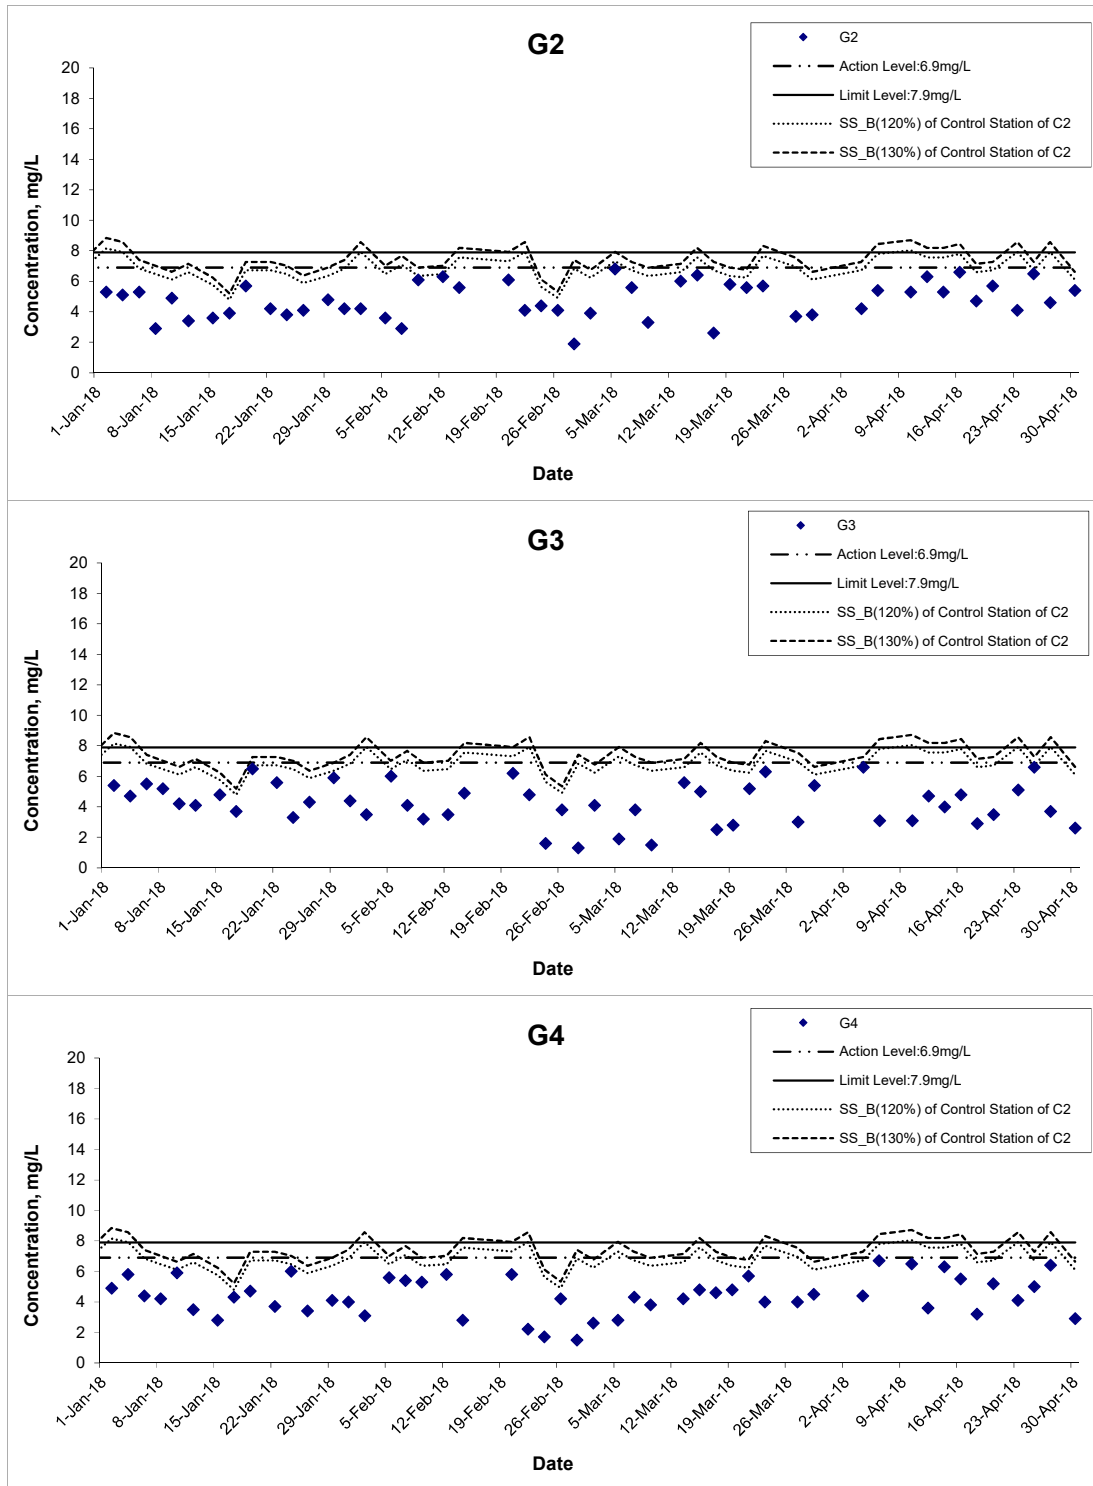

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Ebb Tide

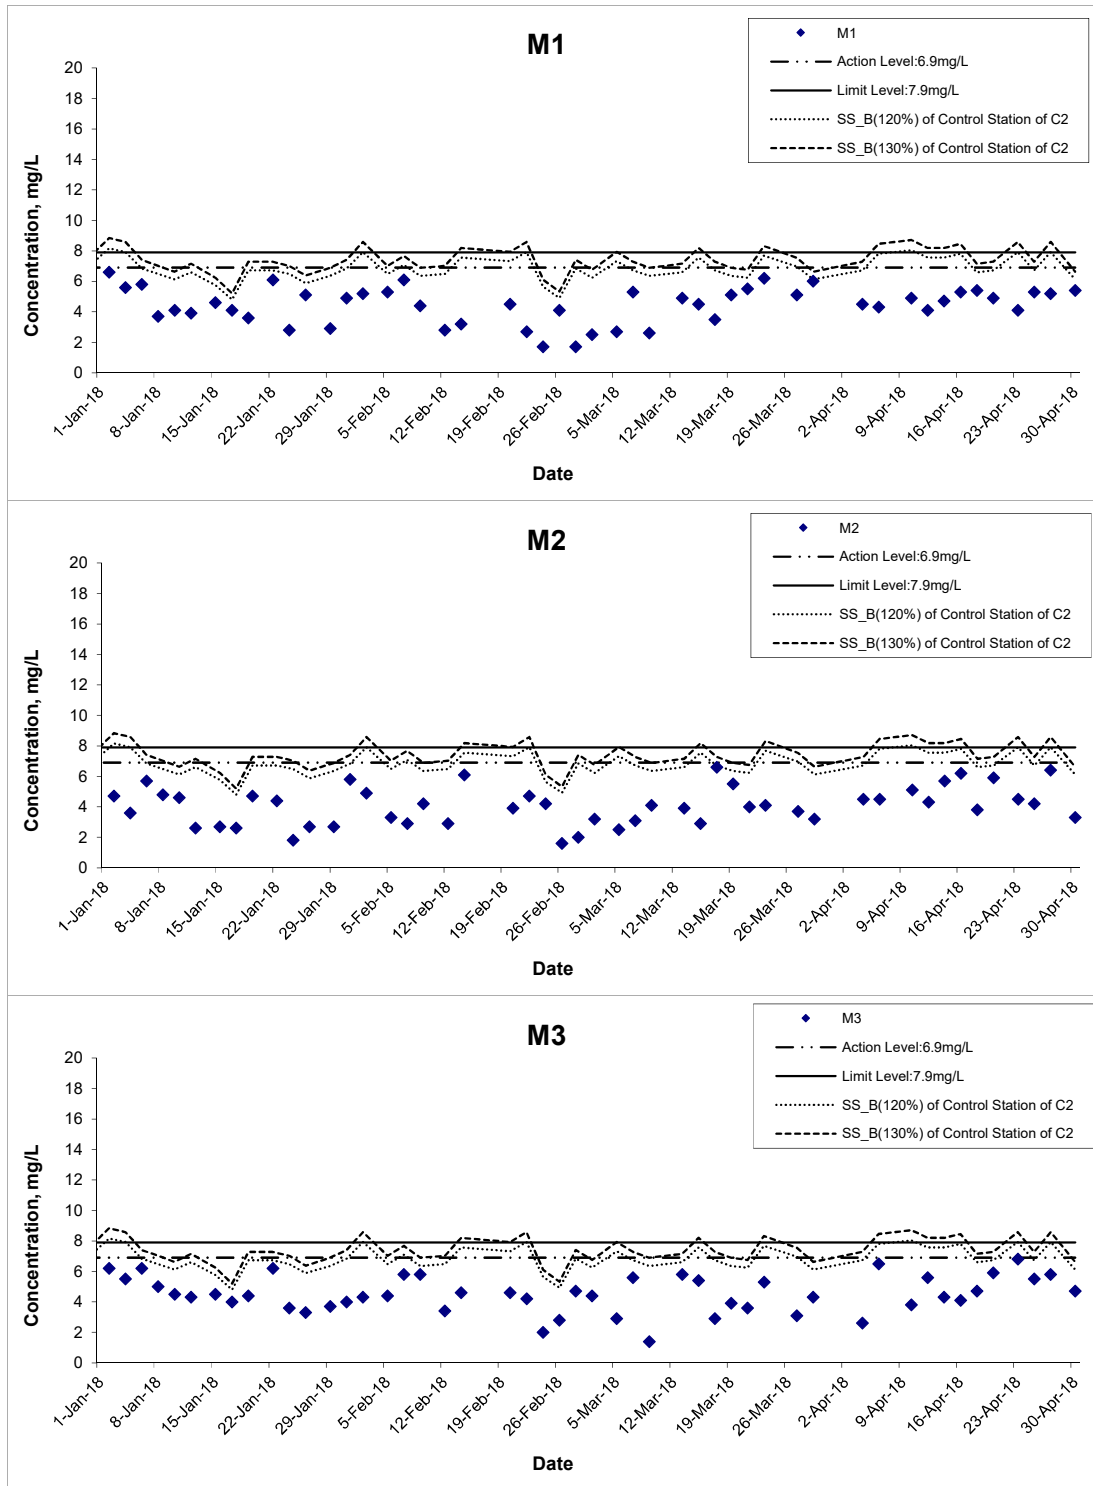

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Ebb Tide

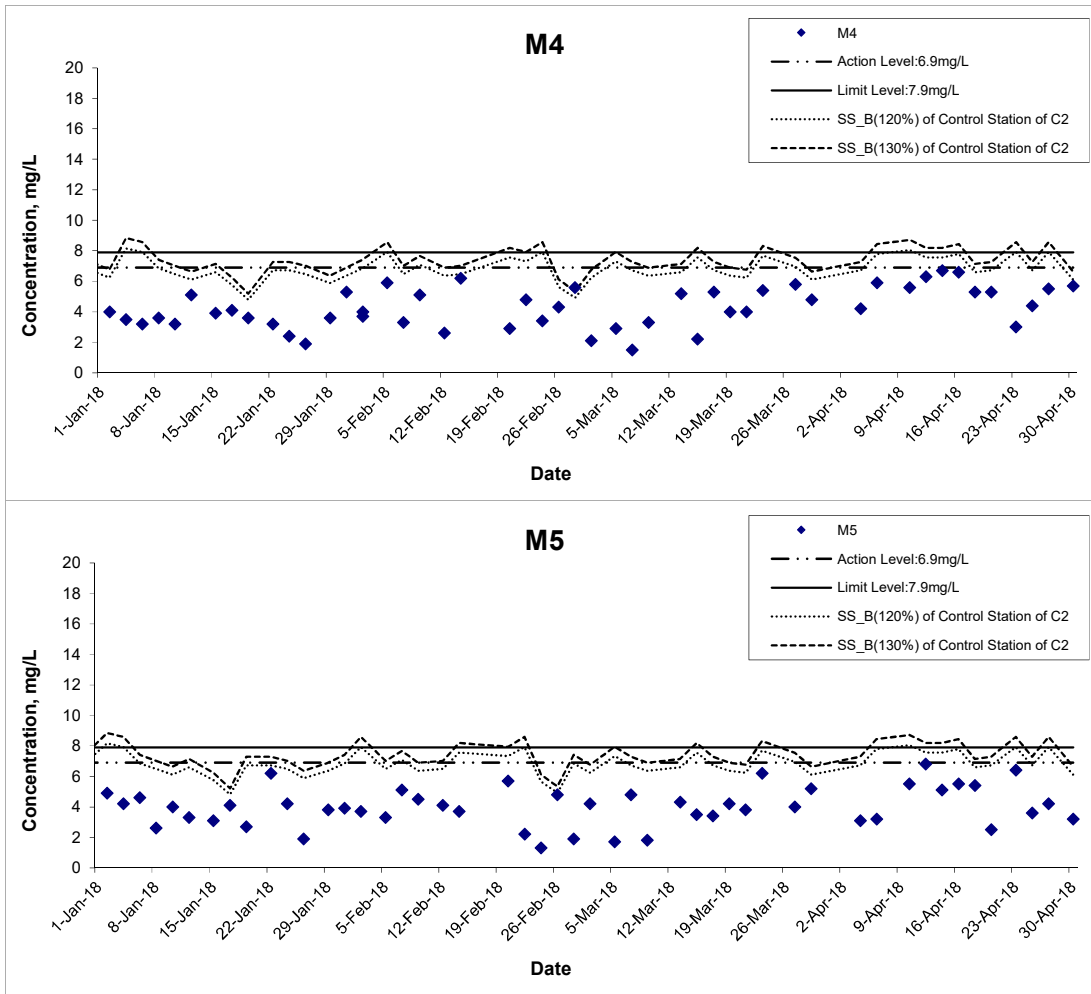

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Flood Tide

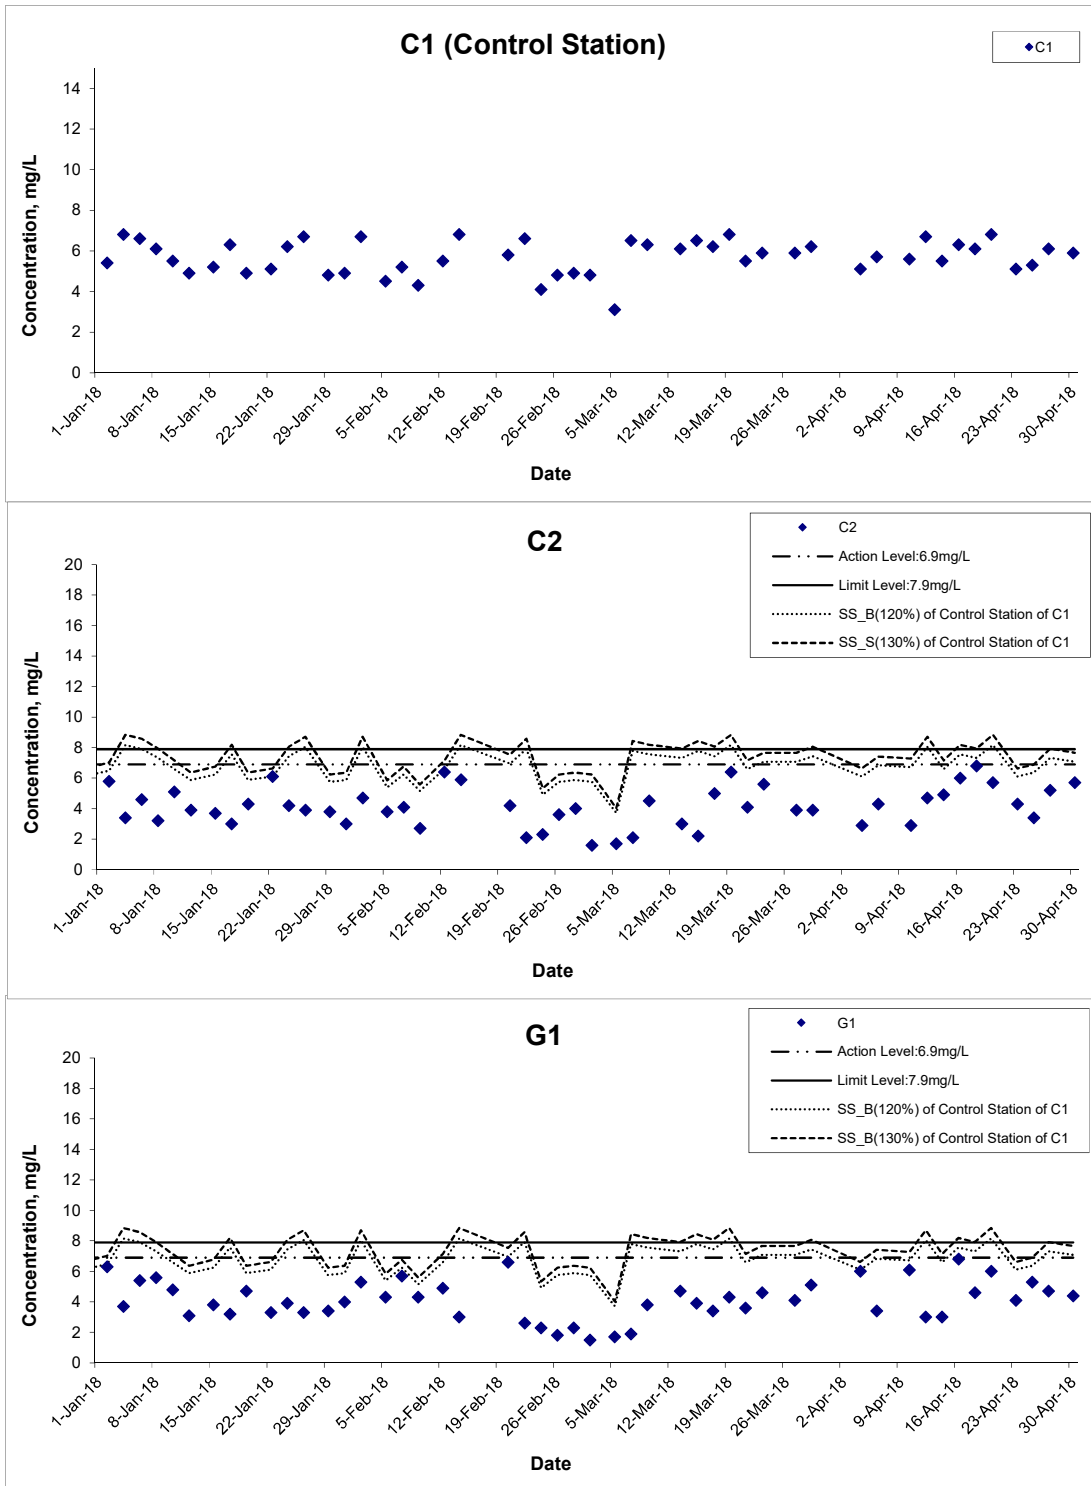

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S




Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Flood Tide

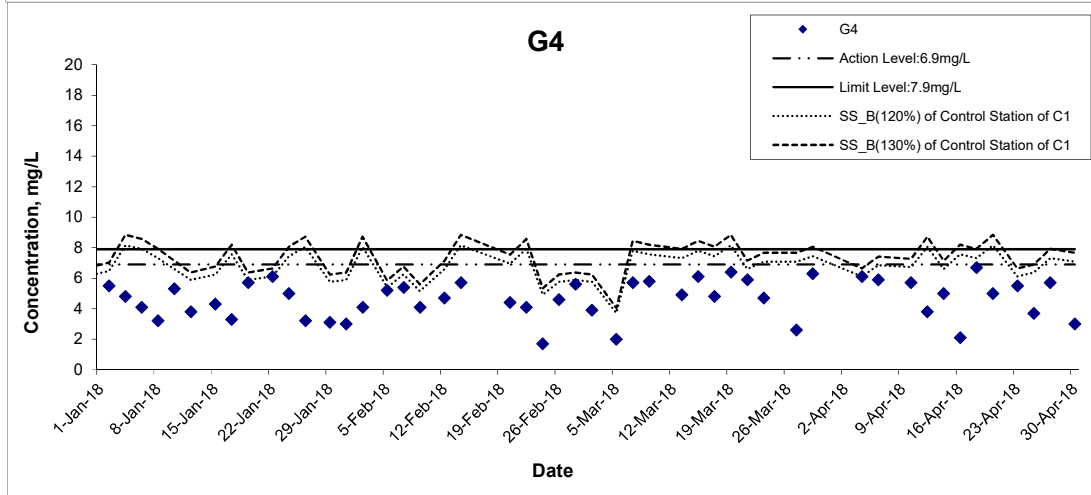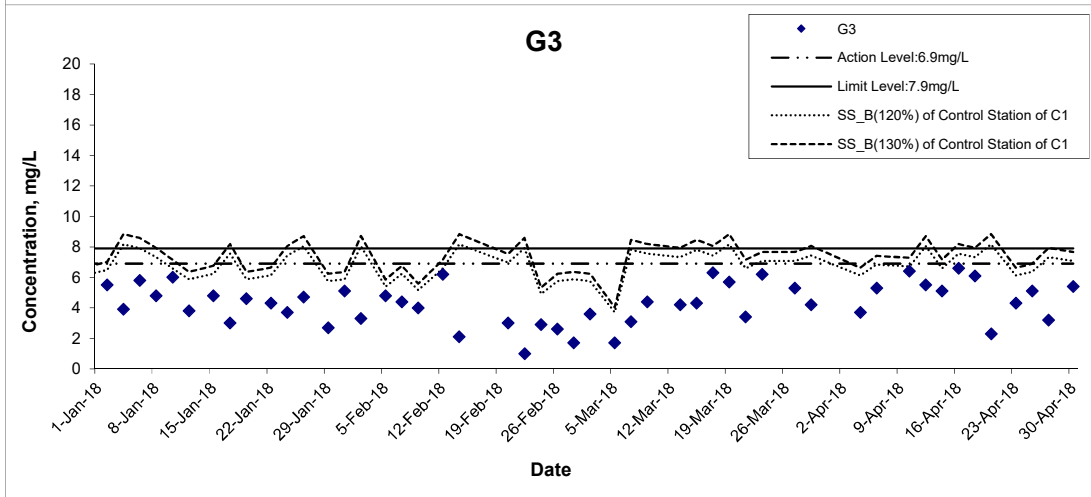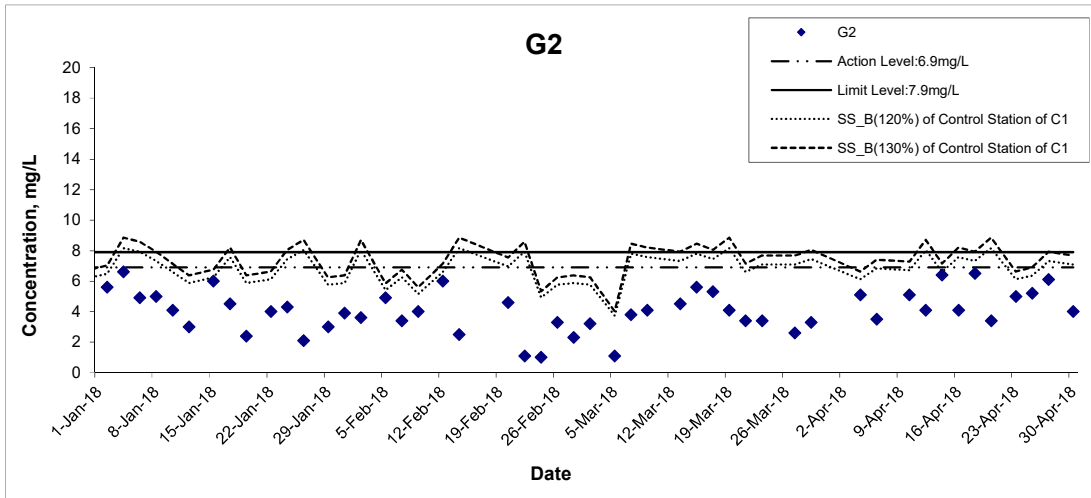

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S




Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Flood Tide

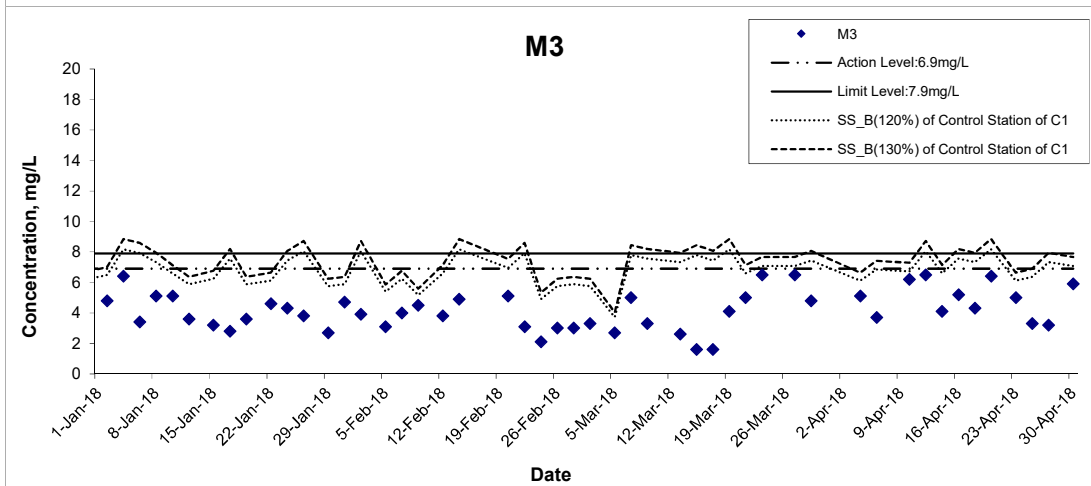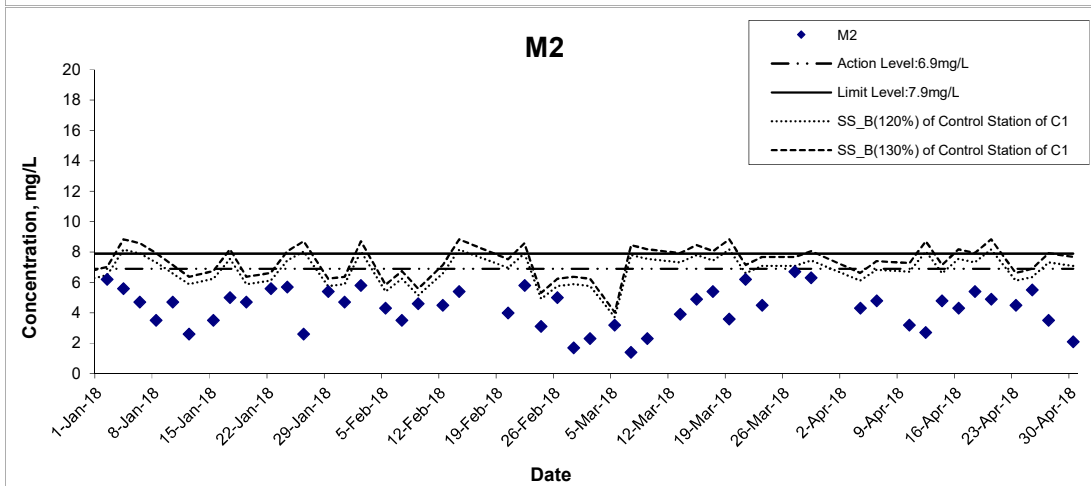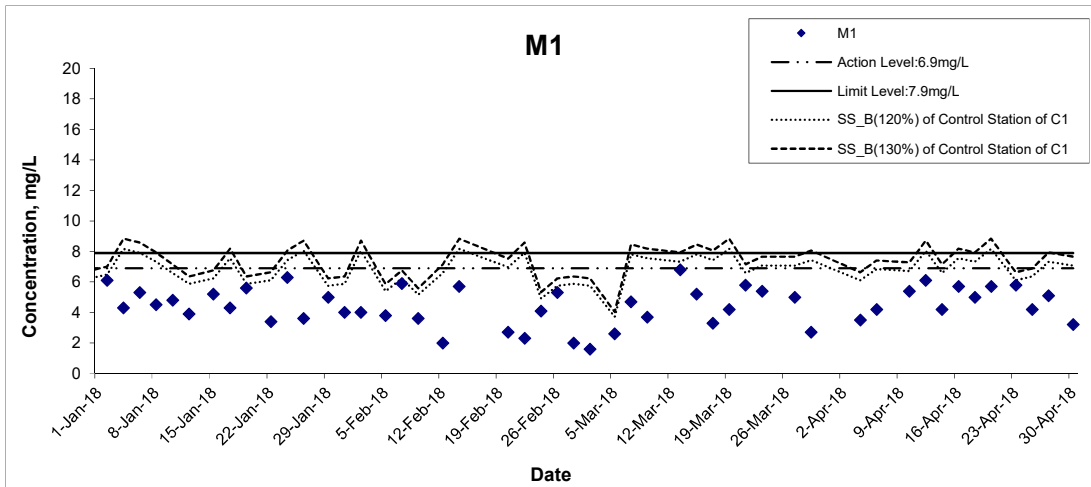

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Bottom) at Mid-Flood Tide

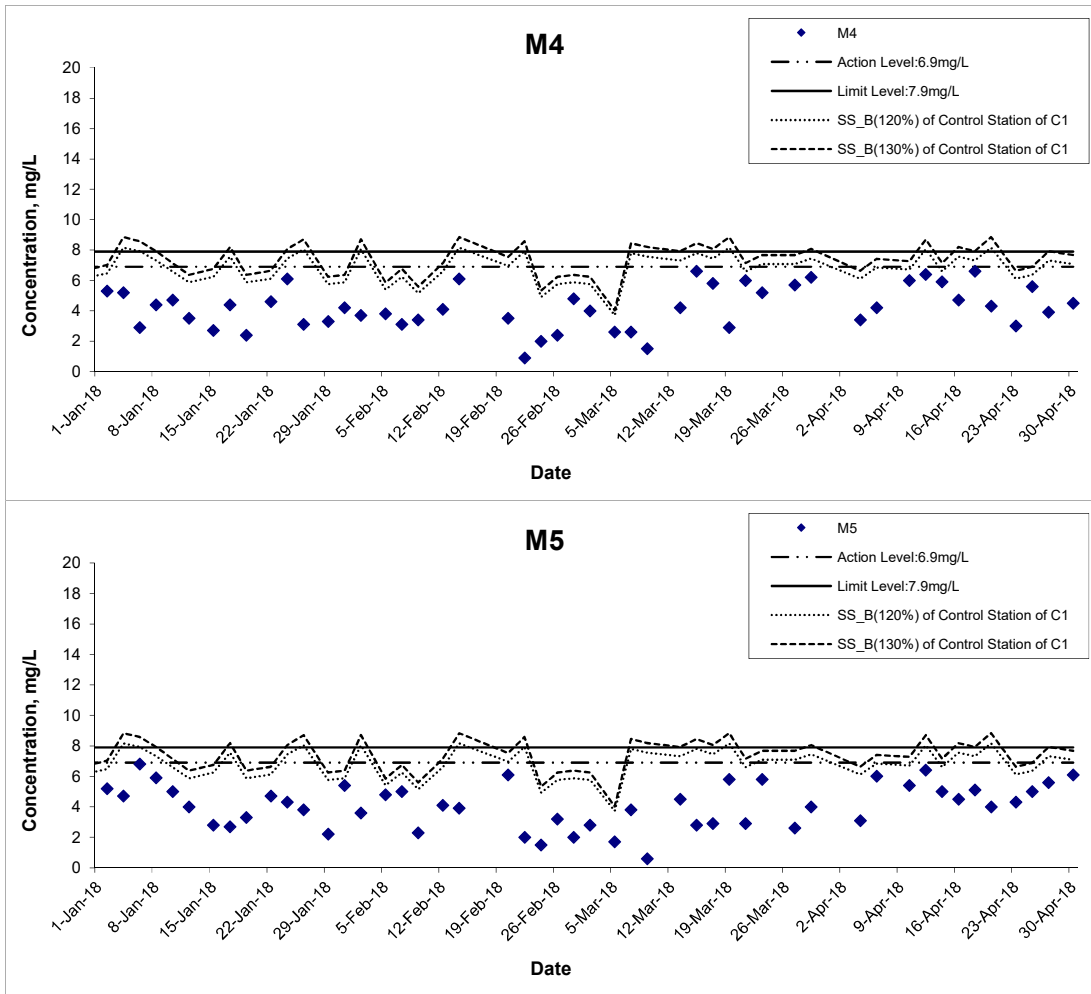

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Intake Level of WSD Salt Water Intake) at Mid-Ebb Tide

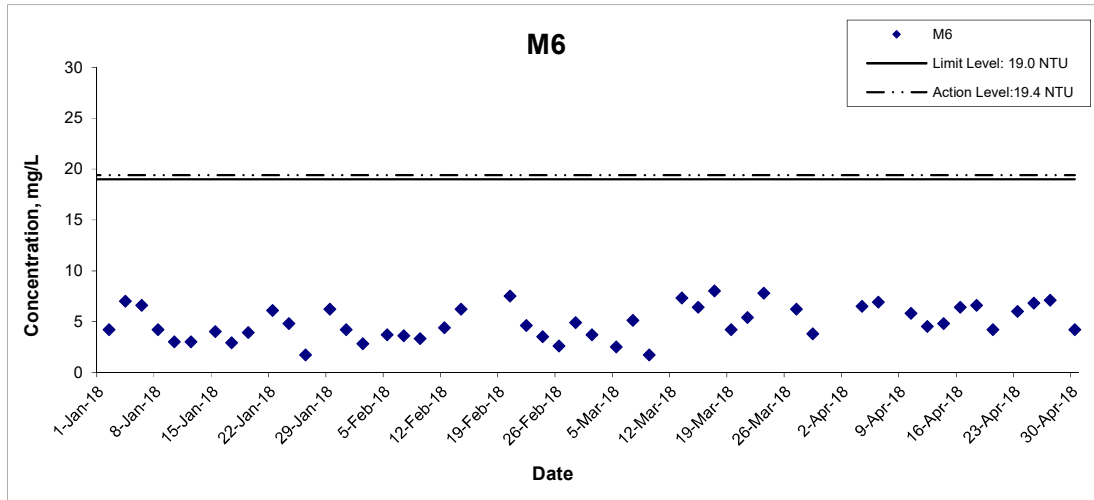

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S


Date Apr 18

Project No. MA16034

Appendix I



Suspended Solids (Intake Level of WSD Salt Water Intake) at Mid-Flood Tide

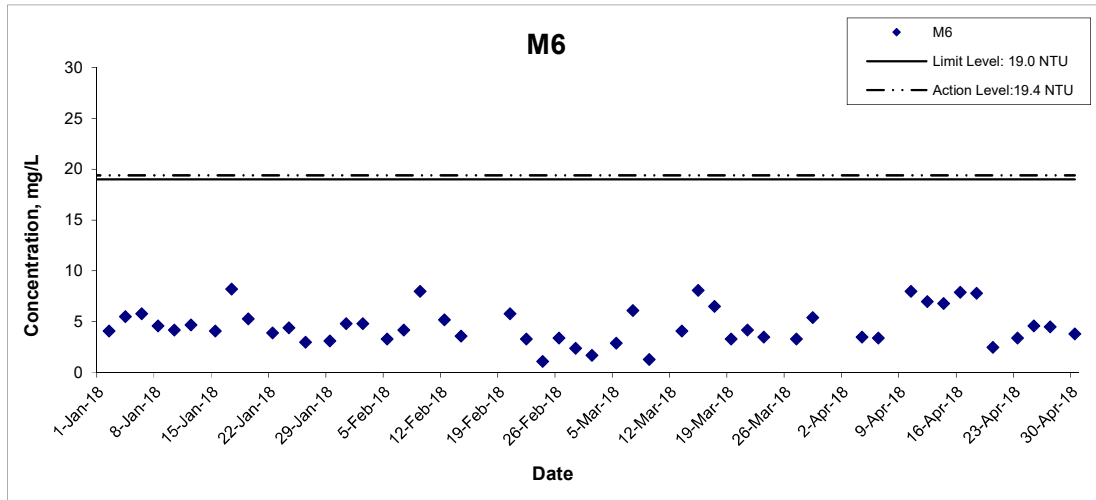

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction

Graphical Presentation of Water Quality Monitoring Results

Scale N.T.S

Date Apr 18

Project No. MA16034

Appendix I



Water Quality Monitoring Results at W1 - Mid-Ebb Tide

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*
6-Apr-18	Cloudy	Calm	16:10	Surface	1	18.8 18.8	18.8	8.2 8.2	8.2	32.3 32.3	32.3	93.2 93.2	93.2	7.3 7.3	7.3	7.3
				Middle	-	-	-	-	-	-	-	-	-	-	-	
				Bottom	3.9	18.6 18.6	18.6	8.2 8.2	8.2	32.3 32.3	32.3	92.1 92.1	92.1	7.2 7.1	7.2	
11-Apr-18	Sunny	Calm	09:29	Surface	1	23.0 23.0	23.0	8.0 8.0	8.0	32.7 32.7	32.7	96.3 96.3	96.3	6.8 6.8	6.8	6.8
				Middle	-	-	-	-	-	-	-	-	-	-	-	
				Bottom	3.8	22.8 22.8	22.8	7.9 7.9	7.9	32.8 32.9	32.9	93.5 93.1	93.3	6.7 6.6	6.7	
19-Apr-18	Sunny	Calm	16:07	Surface	1	23.1 23.0	23.1	8.2 8.3	8.3	33.2 33.2	33.2	86.4 83.3	84.9	6.1 5.9	6.0	6.0
				Middle	-	-	-	-	-	-	-	-	-	-	-	
				Bottom	2.5	23.0 23.0	23.0	8.3 8.3	8.3	33.2 33.2	33.2	82.9 82.5	82.7	5.9 5.9	5.9	
24-Apr-18	Cloudy	Calm	08:52	Surface	1	23.7 23.7	23.7	7.9 7.9	7.9	33.0 33.0	33.0	86.5 86.5	86.5	6.1 6.1	6.1	6.1
				Middle	-	-	-	-	-	-	-	-	-	-	-	
				Bottom	3.6	23.7 23.7	23.7	7.9 7.9	7.9	33.0 33.0	33.0	86.3 86.2	86.3	6.1 6.0	6.1	


Water Quality Monitoring Results at W1 - Mid-Flood Tide

Date	Weather Condition	Sea Condition**	Sampling Time	Depth (m)		Temperature (°C)		pH		Salinity ppt		DO Saturation (%)		Dissolved Oxygen (mg/L)		
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*
6-Apr-18	Cloudy	Calm	09:17	Surface	1	18.8 18.8	18.8	8.1 8.1	8.1	32.3 32.3	32.3	92.9 92.8	92.9	7.3 7.2	7.3	7.3
				Middle	-	-	-	-	-	-	-	-	-	-	-	
				Bottom	4	18.6 18.6	18.6	8.2 8.2	8.2	32.3 32.3	32.3	92.4 92.4	92.4	7.2 7.2	7.2	
11-Apr-18	Sunny	Calm	14:50	Surface	1	23.0 23.1	23.1	8.0 8.0	8.0	32.7 32.7	32.7	95.0 95.8	95.4	6.8 6.8	6.8	6.8
				Middle	-	-	-	-	-	-	-	-	-	-	-	
				Bottom	4	22.7 22.6	22.7	8.0 8.0	8.0	32.7 32.8	32.8	94.7 92.9	93.8	6.8 6.7	6.8	
19-Apr-18	Sunny	Calm	08:50	Surface	1	22.4 22.5	22.5	8.2 8.3	8.3	33.0 33.0	33.0	78.7 78.1	78.4	5.6 5.6	5.6	5.6
				Middle	-	-	-	-	-	-	-	-	-	-	-	
				Bottom	3.1	22.5 22.5	22.5	8.3 8.3	8.3	33.1 33.1	33.1	77.8 77.6	77.7	5.6 5.5	5.6	
24-Apr-18	Cloudy	Calm	12:42	Surface	1	23.7 23.7	23.7	7.9 7.9	7.9	33.0 33.0	33.0	86.7 86.7	86.7	6.1 6.1	6.1	6.1
				Middle	-	-	-	-	-	-	-	-	-	-	-	
				Bottom	3.8	23.7 23.7	23.7	7.9 7.9	7.9	33.0 33.0	33.0	85.7 85.6	85.7	6.0 6.0	6.0	


Remarks: *DA: Depth-Averaged

**Calm: Small or no wave; Moderate: Between calm and rough; Rough : White capped or rougher.

Dissolved Oxygen (Depth-Averaged) at Mid-Ebb Tide

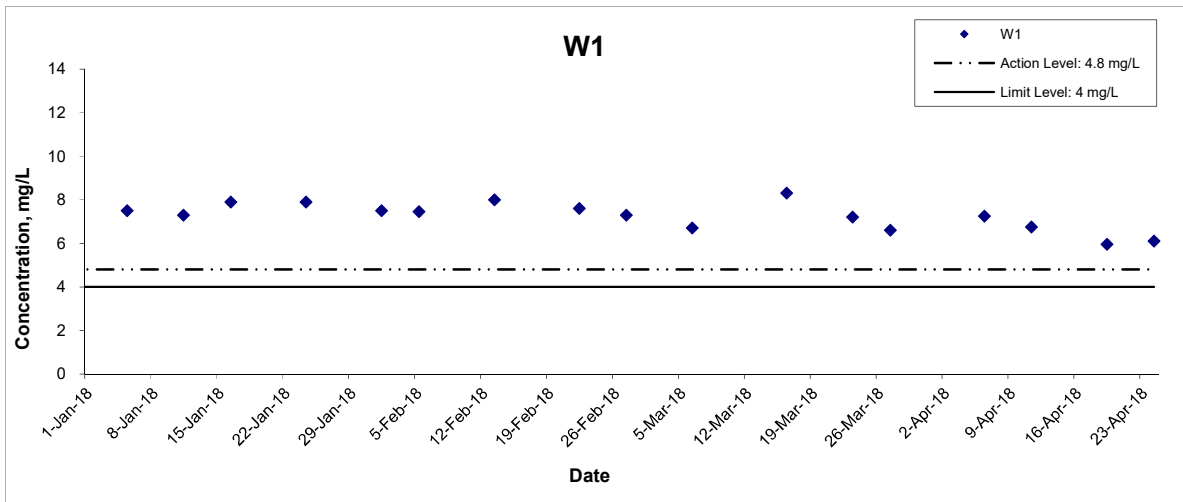

Dissolved Oxygen (Depth-Averaged) at Mid-Flood Tide

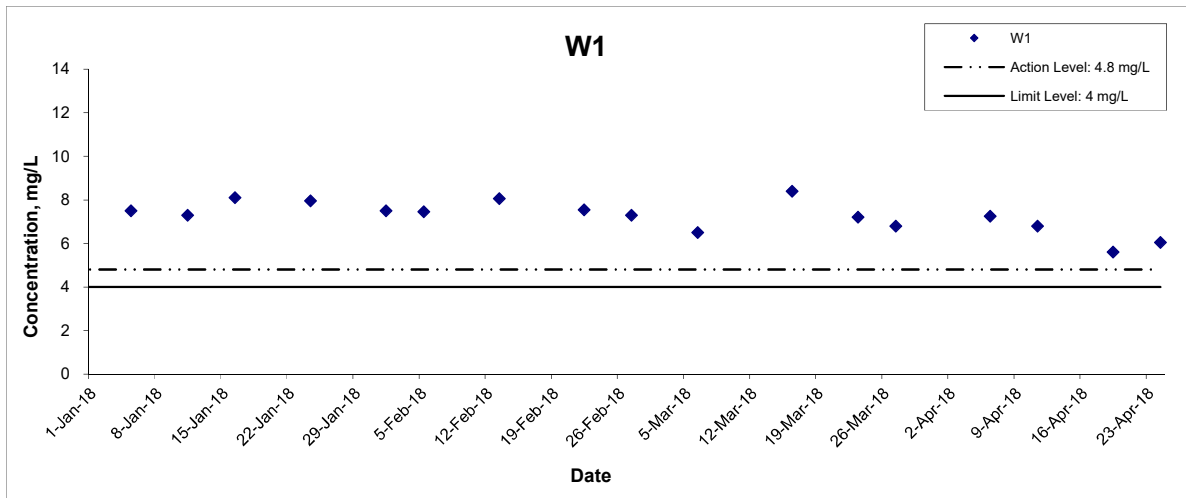


Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Graphical Presentation of Additional Water Quality Monitoring Results

Scale N.T.S
Date Apr 18


Project No. MA16034
Appendix I



Dissolved Oxygen (Bottom) at Mid-Ebb Tide

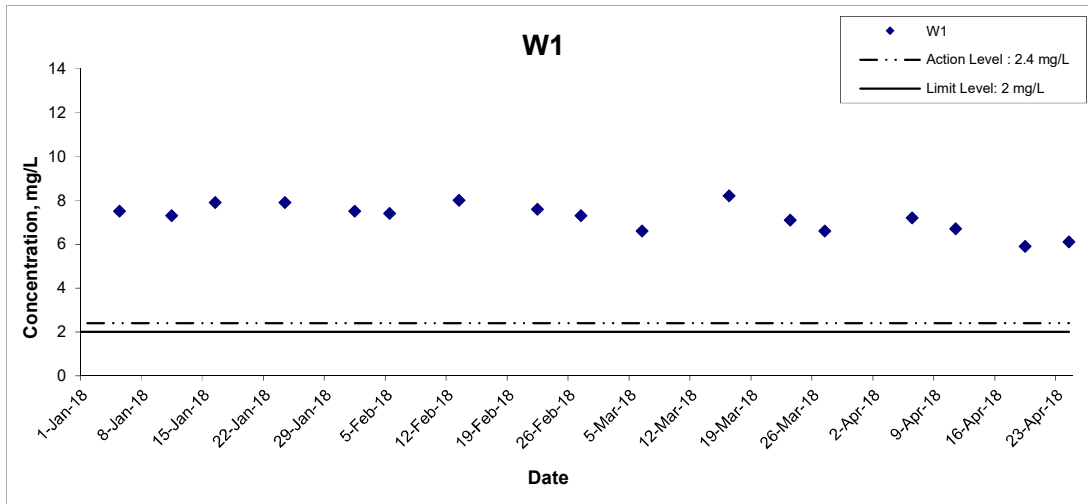

Dissolved Oxygen (Bottom) at Mid-Flood Tide

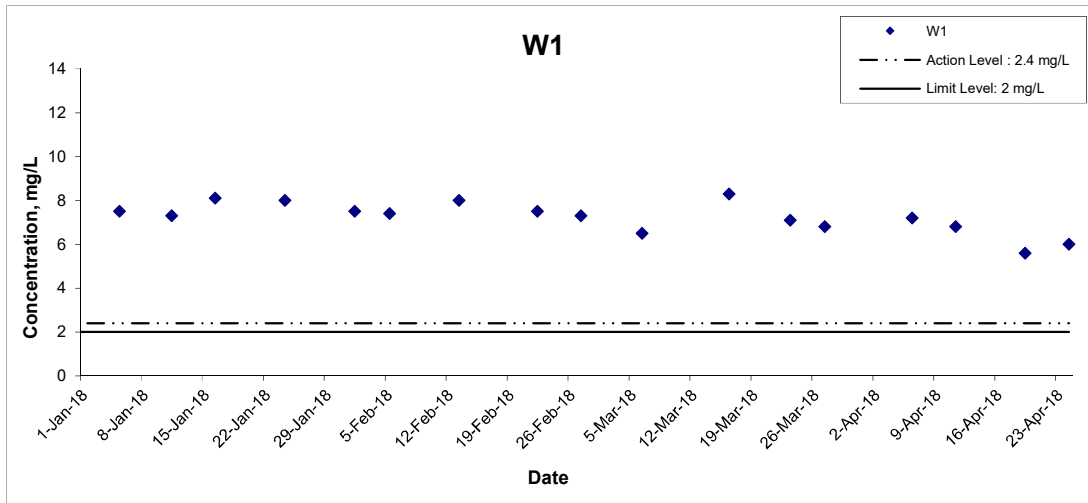

Title Agreement No. CE 59/2015(EP) Environmental Team for Tseung Kwan O - Lam Tin Tunnel Design and Construction
Graphical Presentation of Additional Water Quality Monitoring Results

Scale N.T.S
Date Apr 18

Project No. MA16034
Appendix I



**APPENDIX J
QUALITY CONTROL REPORTS FOR
LABORATORY ANALYSIS**

TEST REPORT

APPLICANT: Cinotech Consultants Limited
1710, Technology Park,
18 On Lai Street,
Shatin, N.T.

Report No.:	QC28692
Date of Issue:	2018-04-20
Date Received:	2018-04-11
Date Tested:	2018-04-11
Date Completed:	2018-04-20

ATTN: Ms. Mei Ling Tang
QC report:

Page: 1 of 2

Method Blank

Parameter	MB 1	Acceptance
Suspended Solids (SS) (mg/L)	<0.5	<0.5
Biochemical Oxygen Demand	N/A	N/A
Total Organic Carbon (mg-TOC/L)	<0.2	<0.2
Nitrogen (Total Kjeldahl + nitrate + nitrite)	N/A	N/A
Ammonia (mg NH ₃ -N/L)	<0.01	<0.01
Total Phosphorus (mg-P/L)	<0.01	<0.01

Method QC

Parameter	MQC1	Acceptance
Suspended Solids (SS) (%)	98	80-120
Biochemical Oxygen Demand (mg O ₂ /L)	196	170-220
Total Organic Carbon (%)	91	80-120
Nitrogen (Total Kjeldahl + nitrate + nitrite)	N/A	N/A
Ammonia (%)	98	80-120
Total Phosphorus (%)	102	80-120

Remarks: 1) <= less than

2) N/A = Not applicable

3) This report is the summary of quality control data for report number 28692.

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

Report No.:	QC28692
Date of Issue:	2018-04-20
Date Received:	2018-04-11
Date Tested:	2018-04-11
Date Completed:	2018-04-20

Page: 2 of 2

QC report:

Sample Duplicate

Parameter	28692-2 chk	Acceptance
Suspended Solids (SS) (%)	1	RPD \leq 20%
Biochemical Oxygen Demand (%)	N/A	RPD \leq 20%
Total Organic Carbon (%)	7	RPD \leq 20%
Nitrogen (Total Kjeldahl + nitrate + nitrite)	N/A	N/A
Ammonia (%)	N/A	RPD \leq 20%
Total Phosphorus (%)	N/A	RPD \leq 20%

Sample Spike

Parameter	28692-2 spk	Acceptance
Suspended Solids (SS) (%)	N/A	N/A
Biochemical Oxygen Demand (%)	N/A	N/A
Total Organic Carbon (%)	94	80-120
Nitrogen (Total Kjeldahl + nitrate + nitrite)	N/A	N/A
Ammonia (%)	93	80-120
Total Phosphorus (%)	96	80-120

Remarks: 1) \leq = less than

2) N/A = Not applicable

3) This report is the summary of quality control data for report number 28692.

*****END OF REPORT*****

TEST REPORT

APPLICANT: Cinotech Consultants Limited
1710, Technology Park,
18 On Lai Street,
Shatin, N.T.

Report No.:	QC28772
Date of Issue:	2018-05-04
Date Received:	2018-04-24
Date Tested:	2018-04-24
Date Completed:	2018-05-04

ATTN: Ms. Mei Ling Tang
QC report:

Page: 1 of 2

Method Blank

Parameter	MB 1	Acceptance
Suspended Solids (SS) (mg/L)	<0.5	<0.5
Biochemical Oxygen Demand	N/A	N/A
Total Organic Carbon (mg-TOC/L)	<0.2	<0.2
Nitrogen (Total Kjeldahl + nitrate + nitrite)	N/A	N/A
Ammonia (mg NH ₃ -N/L)	<0.01	<0.01
Total Phosphorus (mg-P/L)	<0.01	<0.01

Method QC

Parameter	MQC1	Acceptance
Suspended Solids (SS) (%)	95	80-120
Biochemical Oxygen Demand (mg O ₂ /L)	186	170-220
Total Organic Carbon (%)	102	80-120
Nitrogen (Total Kjeldahl + nitrate + nitrite)	N/A	N/A
Ammonia (%)	96	80-120
Total Phosphorus (%)	101	80-120


Remarks: 1) < = less than

2) N/A = Not applicable

3) This report is the summary of quality control data for report number 28772.

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

Report No.:	QC28772
Date of Issue:	2018-05-04
Date Received:	2018-04-24
Date Tested:	2018-04-24
Date Completed:	2018-05-04

Page: 2 of 2

QC report:

Sample Duplicate

Parameter	28772-3 chk	Acceptance
Suspended Solids (SS) (%)	3	RPD \leq 20%
Biochemical Oxygen Demand (%)	3	RPD \leq 20%
Total Organic Carbon (%)	2	RPD \leq 20%
Nitrogen (Total Kjeldahl + nitrate + nitrite)	N/A	N/A
Ammonia (%)	2	RPD \leq 20%
Total Phosphorus (%)	2	RPD \leq 20%

Sample Spike

Parameter	28772-3 spk	Acceptance
Suspended Solids (SS) (%)	N/A	N/A
Biochemical Oxygen Demand (%)	N/A	N/A
Total Organic Carbon (%)	100	80-120
Nitrogen (Total Kjeldahl + nitrate + nitrite)	N/A	N/A
Ammonia (%)	101	80-120
Total Phosphorus (%)	93	80-120

Remarks: 1) \leq less than

2) N/A = Not applicable

3) This report is the summary of quality control data for report number 28772.

*****END OF REPORT*****

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28657
Date of Issue:	2018/4/6
Date Received:	2018/4/4
Date Tested:	2018/4/4
Date Completed:	2018/4/6

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2018/4/4

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/180404

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	4.0	4.0	0	107

*****END OF REPORT*****

PREPARED AND CHECKED BY:

For and On Behalf of WELLAB Ltd.



PATRICK TSE

Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28665
Date of Issue:	2018/4/9
Date Received:	2018/4/6
Date Tested:	2018/4/6
Date Completed:	2018/4/9

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)
Project No.: MA16034
Sampling Date: 2018/4/6
Number of Sample: 136
Custody No.: MA16034-CE/59/2015(EP)/180406

Total Suspended Solids Sampling Point	Duplicate Analysis			QC Recovery, %
	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	3.7	3.5	5	102

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28676
Date of Issue:	2018/4/11
Date Received:	2018/4/10
Date Tested:	2018/4/10
Date Completed:	2018/4/11

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2018/4/10

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/180410

Total Suspended Solids Sampling Point	Duplicate Analysis			QC Recovery, %
	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	4.2	4.5	7	97

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of WELLAB Ltd.



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28686
Date of Issue:	2018/4/13
Date Received:	2018/4/12
Date Tested:	2018/4/12
Date Completed:	2018/4/13

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)
Project No.: MA16034
Sampling Date: 2018/4/12
Number of Sample: 136
Custody No.: MA16034-CE/59/2015(EP)/180412

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	4.1	4.3	6	107

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of WELLAB Ltd.



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28700
Date of Issue:	2018/4/16
Date Received:	2018/4/14
Date Tested:	2018/4/14
Date Completed:	2018/4/16

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2018/4/14

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/180414

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	5.2	5.5	6	104

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of WELLAB Ltd.



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28706
Date of Issue:	2018/4/17
Date Received:	2018/4/16
Date Tested:	2018/4/16
Date Completed:	2018/4/17

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2018/4/16

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/180416

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	5.5	5.6	2	102

*****END OF REPORT*****

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE

Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28719
Date of Issue:	2018/4/19
Date Received:	2018/4/18
Date Tested:	2018/4/18
Date Completed:	2018/4/19

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2018/4/18

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/180418

Total Suspended Solids Sampling Point	Duplicate Analysis			QC Recovery, %
	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	4.8	4.7	3	106

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of WELLAB Ltd.



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28738
Date of Issue:	2018/4/23
Date Received:	2018/4/20
Date Tested:	2018/4/20
Date Completed:	2018/4/23

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2018/4/20

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/180420

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	4.8	4.9	4	98

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28747
Date of Issue:	2018/4/24
Date Received:	2018/4/23
Date Tested:	2018/4/23
Date Completed:	2018/4/24

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2018/4/23

Number of Sample: 136


Custody No.: MA16034-CE/59/2015(EP)/180423

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	4.6	4.5	2	100

*****END OF REPORT*****

PREPARED AND CHECKED BY:

For and On Behalf of **WELLAB Ltd.**



PATRICK TSE

Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28765
Date of Issue:	2018/4/26
Date Received:	2018/4/25
Date Tested:	2018/4/25
Date Completed:	2018/4/26

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)
Project No.: MA16034
Sampling Date: 2018/4/25
Number of Sample: 136
Custody No.: MA16034-CE/59/2015(EP)/180425

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	4.8	4.6	2	107

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28784
Date of Issue:	2018/4/30
Date Received:	2018/4/27
Date Tested:	2018/4/27
Date Completed:	2018/4/30

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2018/4/27

Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)/180427

Total Suspended Solids	Duplicate Analysis			QC Recovery, %
Sampling Point	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	4.4	4.4	1	95

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

TEST REPORT

QC REPORT

APPLICANT: Cinotech Consultants Limited
RM 1710, Technology Park,
18 On Lai Street,
Shatin, N.T., Hong Kong

Report No.:	28801
Date of Issue:	2018/5/2
Date Received:	2018/4/30
Date Tested:	2018/4/30
Date Completed:	2018/5/2

ATTN: Ms. Mei Ling Tang

Page: 1 of 1

Project Name: Enviromental Team for Tseung Kwan O - Lam Tin Tunnel -
Design and Construction Agreement No. CE/59/2015 (EP)

Project No.: MA16034

Sampling Date: 2018/4/30


Number of Sample: 136

Custody No.: MA16034-CE/59/2015(EP)180430

Total Suspended Solids Sampling Point	Duplicate Analysis			QC Recovery, %
	Trial 1, mg/L	Trial 2, mg/L	Difference, %	
M4se	5.7	5.6	2	101

*****END OF REPORT*****

PREPARED AND CHECKED BY:
For and On Behalf of **WELLAB Ltd.**



PATRICK TSE
Laboratory Manager

**APPENDIX K
SUMMARY OF EXCEEDANCE**

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel –
Design and Construction

Appendix K – Summary of Exceedance

Reporting Period: April 2018

(A) Exceedance Report for Air Quality
(NIL in the reporting month)

(B) Exceedance Report for Construction Noise

Action Level for Construction Noise

(Thirteen (13) Action Level exceedances were recorded due to the documented complaints received in this reporting month.)

Limit Level for Construction Noise

(NIL in the reporting month)

(C) Exceedance Report for Water Quality

(No exceedance for marine water quality monitoring in the reporting month)

(One Action Level and Twelve Limit Level exceedances in groundwater quality monitoring as followed:

Date	Monitoring Location	Monitoring Parameter	Monitoring Results	Action Level	Limit Level
24 April 2018	Stream 1	Biochemical Oxygen Demand	4 mg O ₂ /L	2.0	2.0
24 April 2018	Stream 1	Total Organic Carbon	12 mg-TOC/L	9	9
24 April 2018	Stream 1	Total Nitrogen	3.7 mg N/L	2.0	2.1
24 April 2018	Stream 1	Total Phosphorus	0.06 mg-P/L	0.05	0.05
24 April 2018	Stream 2	Biochemical Oxygen Demand	8 mg O ₂ /L	2.0	2.0
24 April 2018	Stream 2	Total Organic Carbon	16 mg-TOC/L	9	9
24 April 2018	Stream 2	Total Nitrogen	2.9 mg N/L	2.0	2.1
24 April 2018	Stream 2	Total Phosphorus	0.08 mg-P/L	0.05	0.05
24 April 2018	Stream 3	Biochemical Oxygen Demand	4 mg O ₂ /L	2.0	2.0
24 April 2018	Stream 3	Total Organic Carbon	8 mg-TOC/L	6	6
24 April 2018	Stream 3	Total Nitrogen	2.9 mg N/L	2.0	2.1
24 April 2018	Stream 3	Ammonia-N	0.16 mg NH ₃ -N/L	0.15	0.20
24 April 2018	Stream 3	Total Phosphorus	0.1 mg-P/L	0.05	0.05

Note: The exceedance for groundwater quality recorded on 24 April 2018 is still under investigation.

(D) Exceedance Report for Ecology
(NIL in the reporting month)

(E) Exceedance Report for Cultural Heritage

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel –
Design and Construction

Appendix K – Summary of Exceedance
(NIL in the reporting month)

(F) Exceedance Report for Landfill Gas
(NIL in the reporting month)

**APPENDIX L
SITE AUDIT SUMMARY**

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction
Monthly EM&A Report

Appendix L - Site Audit Summary (April 2018)

Contract No. NE/2015/01

Tseung Kwan O - Lam Tin Tunnel - Main Tunnel and Associated Works

Items	Date	Status*	Follow up Action
Water Quality			
Gaps between silt curtains in TKO site should be avoided.	28 March 2018	✓	Improved/rectified on 4 April 2018.
Silt curtain near marine platform in TKO site should be maintained to prevent untreated discharge.	25 April 2018	#	Follow up action will be reported in next reporting month
Noise			
--	--	--	--
Landscape and Visual			
--	--	--	--
Air Quality			
Water spraying should be provided to slopes in LTI for dust suppression.	28 March 2018	✓	Improved/rectified on 4 April 2018.
NRMM labels should be properly displayed on PMEs in Portion 6 in TKO site.	11 April 2018	✓	Improved/rectified on 18 April 2018
Water spraying should be provided to slopes in LTI more frequently for dust suppression.	18 April 2018	✓	Improved/rectified on 25 April 2018
Water sprinklers on Slope H should be provided to all breaking works for dust suppression.	25 April 2018	#	Follow up action will be reported in next reporting month
Waste / Chemical Management			
Drip tray should be provided to chemical containers in WA1.	4 April 2018	✓	Improved/rectified on 11 April 2018.
PME in Portion 6 in TKO site should be maintained regularly to avoid oil leakage.	11 April 2018	✓	Improved/rectified on 18 April 2018
Impact on Cultural Heritage			
--	--	--	--
Permits / Licenses			
--	--	--	--

- ✓ Observation/reminder was made during site audit but improved/rectified by the contractor in the next site audit
- ✗ Observation/reminder was made during site audit but not yet improved/rectified by the contractor in the next site audit
- # Follow up action will be reported in next reporting month
- * Non-compliance of mitigation measure
- Non-compliance but improved by the contractor

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction
Monthly EM&A Report

Appendix L - Site Audit Summary (April 2018)

Contract No. NE/2015/02

Tseung Kwan O - Lam Tin Tunnel - Road P2 and Associated Works

Items	Date	Status*	Follow up Action
<i>Water Quality</i>			
Silt curtains near the double water gate are observed damaged. The Contractor should maintain the silt curtains properly and ensure the geotextile is extended to seabed.	22 March 2018	✗	Item remarked on 29 March 2018.
	29 March 2018	✓	Improved/rectified on 6 April 2018.
To repair the damaged silt curtain at the double water gate and deploy silt curtains around the cofferdam properly without gaps.	26 April 2018	#	Follow up action will be reported in next reporting month
The Contractor was reminded to clear the sediment at the unloading area at Portion 7 regularly.	26 April 2018	#	Follow up action will be reported in next reporting month
<i>Noise</i>			
The Contractor was reminded to properly erect noise barriers for the drill rig in Portion 7 to reduce noise nuisance to nearby NSR.	17 April 2018	✓	Improved/rectified on 26 April 2018.
To place the acoustic box properly for breaking work in Portion 4.	26 April 2018	#	Follow up action will be reported in next reporting month
The Contractor was reminded to erect an effective acoustic mat for the derrick barge at the unloading area in Portion 7 and properly erect the noise barrier near the entrance of Portion 7.	26 April 2018	#	Follow up action will be reported in next reporting month
The Contractor was reminded to replace NRMM labels when needed.	26 April 2018	#	Follow up action will be reported in next reporting month
<i>Landscape and Visual</i>			
--	--	--	--
<i>Air Quality</i>			
Haul road at Portion 4 was observed dry. The Contractor should provide sufficient water spraying for dust suppression.	29 March 2018	✓	Improved/rectified on 6 April 2018.
The Contractor was reminded to repair the retractable tube of the drill rig in Portion 4 and ensure its integrity at all time.	12 April 2018	✓	Improved/rectified on 17 April 2018.
The Contractor was reminded to provide water spraying for unloading / loading activity at Portion 5	26 April 2018	#	Follow up action will be reported in next reporting month
The Contractor was reminded to maintain the construction vessels regularly to prevent black smoke emission.	26 April 2018	#	Follow up action will be reported in next reporting month
The Contractor was reminded to lower the level of stockpiles in Work Area A and cover them with impervious sheet.	26 April 2018	#	Follow up action will be reported in next reporting month
<i>Waste / Chemical Management</i>			
To clear the oil stain found under the pre-boring machine in Portion 5.	29 March 2018	✓	Improved/rectified on 6 April 2018.
The Contractor was reminded to properly clear the oil stain at the double water gate and Portion 4.	26 April 2018	#	Follow up action will be reported in next reporting month
<i>Impact on Cultural Heritage</i>			
--	--	--	--
<i>Permits / Licenses</i>			

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction
Monthly EM&A Report

Appendix L - Site Audit Summary (April 2018)

Items	Date	Status*	Follow up Action
--	--	--	--

- ✓ Observation/reminder was made during site audit but improved/rectified by the contractor in the next site audit
- ✗ Observation/reminder was made during site audit but not yet improved/rectified by the contractor in the next site audit
- # Follow up action will be reported in next reporting month

- * Non-compliance of mitigation measure
- Non-compliance but rectified by the contractor

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction
Monthly EM&A Report

Appendix L - Site Audit Summary (April 2018)

Contract No. NE/2015/03

Tseung Kwan O - Lam Tin Tunnel - Northern Footbridge

Items	Date	Status*	Follow up Action
<i>Water Quality</i>			
Water leakage was found in the sedimentation tank in West Pier. The Contractor was reminded to rectify immediately and check the performance regularly	27 April 2018	#	Follow up action will be reported in next reporting month
<i>Noise</i>			
--	--	--	--
<i>Landscape and Visual</i>			
--	--	--	--
<i>Air Quality</i>			
--	--	--	--
<i>Waste / Chemical Management</i>			
--	--	--	--
<i>Impact on Cultural Heritage</i>			
--	--	--	--
<i>Permits / Licenses</i>			
--	--	--	--

- ✓ Observation/reminder was made during site audit but improved/rectified by the contractor in the next site audit
- ✗ Observation/reminder was made during site audit but not yet improved/rectified by the contractor in the next site audit
- # Follow up action will be reported in next reporting month

- * Non-compliance of mitigation measure
- Non-compliance but rectified by the contractor

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction
Monthly EM&A Report

Appendix L - Site Audit Summary (April 2018)

Contract No. NE/2017/01

Tseung Kwan O - Lam Tin Tunnel – Tsueng Kwan O Interchange and Associated Works

Items	Date	Status*	Follow up Action
<i>Water Quality</i>			
--	--	--	--
<i>Noise</i>			
--	--	--	--
<i>Landscape and Visual</i>			
--	--	--	--
<i>Air Quality</i>			
--	--	--	--
<i>Waste / Chemical Management</i>			
--	--	--	--
<i>Impact on Cultural Heritage</i>			
--	--	--	--
<i>Permits / Licenses</i>			

- ✓ Observation/reminder was made during site audit but improved/rectified by the contractor in the next site audit
- ✗ Observation/reminder was made during site audit but not yet improved/rectified by the contractor in the next site audit
- # Follow up action will be reported in next reporting month
- * Non-compliance of mitigation measure
- Non-compliance but rectified by the contractor

Agreement No. CE 59/2015 (EP)
Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction
Monthly EM&A Report

Appendix L - Site Audit Summary (April 2018)

Contract No. NE/2017/02

Tseung Kwan O - Lam Tin Tunnel – Road P2/D4 and Associated Works

Items	Date	Status*	Follow up Action
<i>Water Quality</i>			
--	--	--	--
<i>Noise</i>			
--	--	--	--
<i>Landscape and Visual</i>			
--	--	--	--
<i>Air Quality</i>			
Dusty materials should be removed to prevent dust generation.	30 April 2018	#	Follow up action will be reported in next reporting month
<i>Waste / Chemical Management</i>			
General refuse should be collected and disposed regularly.	04 April 2018	✓	Improved/rectified on 9 April 2018.
<i>Impact on Cultural Heritage</i>			
--	--	--	--
<i>Permits / Licenses</i>			

- ✓ Observation/reminder was made during site audit but improved/rectified by the contractor in the next site audit
- ✗ Observation/reminder was made during site audit but not yet improved/rectified by the contractor in the next site audit
- # Follow up action will be reported in next reporting month

- * Non-compliance of mitigation measure
- Non-compliance but rectified by the contractor

APPENDIX M
EVENT AND ACTION PLANS

Event and Action Plan for Air Quality (Dust)

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action level being exceeded by one sampling	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of complaint and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Action level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial actions to IEC within three working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
	8. If exceedance stops, cease additional monitoring.			
Limit level being exceeded by one sampling	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform Contractor ,IEC, ER, and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within three working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
Limit level being exceeded by two or more consecutive sampling	<ol style="list-style-type: none"> 1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within three working days of notification; 3. Implement the agreed proposals;

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
	5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	3. Supervise the implementation of remedial measures.	4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Event and Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level	<ol style="list-style-type: none"> 1. Notify IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC; 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC, ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances; 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
	7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.			

Event and Action Plan for Marine Water Quality

Event	Action			
	ET	IEC	ER	CONTRACTOR
Action level being exceeded by one sampling day at water sensitive receiver(s)	<ul style="list-style-type: none"> Identify the source(s) of impact by comparing the results with those collected at the control stations as appropriate; If exceedance is found to be caused by the reclamation activities, repeat <i>in-situ</i> measurement to confirm findings; Inform IEC and contractor; Check monitoring data, all plant, equipment and Contractor's working methods; If exceedance occurs at WSD salt water intake, inform WSD; Discuss mitigation measures with IEC and Contractor; Repeat measurement on next day of exceedance. 	<ul style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; Review proposal on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation proposal. 	<ul style="list-style-type: none"> Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Amend working methods if appropriate; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agree mitigation measures.
Action level being exceeded by two or more consecutive	<ul style="list-style-type: none"> Identify the source(s) of impact by comparing the results with those collected at the control stations as appropriate; 	<ul style="list-style-type: none"> Discuss with ET and Contractor on the mitigation measures; 	<ul style="list-style-type: none"> Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation proposal; 	<ul style="list-style-type: none"> Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice;

Event	Action			
	ET	IEC	ER	CONTRACTOR
sampling days at water sensitive receiver(s)	<ul style="list-style-type: none"> • If exceedance is found to be caused by the reclamation activities, repeat in-situ measurement to confirm findings; • Inform IEC and contractor; • Check monitoring data, all plant, equipment and Contractor's working methods; • Discuss mitigation measures with IEC and Contractor; • Ensure mitigation measures are implemented; • Prepare to increase the monitoring frequency to daily; • If exceedance occurs at WSD salt water intake, inform WSD; • Repeat measurement on next day of exceedance. 	<ul style="list-style-type: none"> • Review proposal on mitigation measures submitted by Contractor and advise the ER accordingly; • Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> • Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> • Check all plant and equipment and consider changes of working methods; • Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; • Implement the agreed mitigation measures.
Limit level being exceeded by one sampling day at water sensitive receiver(s)	<ul style="list-style-type: none"> • Identify the source(s) of impact by comparing the results with those collected at the control stations as appropriate; 	<ul style="list-style-type: none"> • Discuss with ET and Contractor on the mitigation measures; • Review proposal on mitigation measures submitted by Contractor and advise the ER accordingly; 	<ul style="list-style-type: none"> • Discuss with IEC, ET and Contractor on the proposed mitigation measures; • Request Contractor to critically review the working methods; 	<ul style="list-style-type: none"> • Inform the ER and confirm notification of the non-compliance in writing; • Rectify unacceptable practice;

Event	Action			
	ET	IEC	ER	CONTRACTOR
	<ul style="list-style-type: none"> • If exceedance is found to be caused by the reclamation activities, repeat <i>in-situ</i> measurement to confirm findings; • Inform IEC, contractor, AFCD and EPD • Check monitoring data, all plant, equipment and Contractor's working methods; • Discuss mitigation measures with IEC, ER and Contractor; • Ensure mitigation measures are implemented; • Increase the monitoring frequency to daily until no exceedance of Limit level; • If exceedance occurs at WSD salt water intake, inform WSD. 	<ul style="list-style-type: none"> • Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> • Make agreement on the mitigation measures to be implemented; • Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> • Check all plant and equipment and consider changes of working methods; • Discuss with ET, IEC and ER and submit proposal of mitigation measures to IEC and ER within 3 working days of notification; • Implement the agreed mitigation measures.
Limit level being exceeded by two or more consecutive sampling days at	<ul style="list-style-type: none"> • Identify the source(s) of impact by comparing the results with those collected at the control stations as appropriate; 	<ul style="list-style-type: none"> • Discuss with ET and Contractor on the mitigation measures; • Review proposal on mitigation measures submitted by Contractor and advise the ER accordingly; 	<ul style="list-style-type: none"> • Discuss with IC(E), ET and Contractor on the proposed mitigation measures; • Request Contractor to critically review the working methods; 	<ul style="list-style-type: none"> • Inform the ER and confirm notification of the non-compliance in writing; • Rectify unacceptable practice;

Event	Action			
	ET	IEC	ER	CONTRACTOR
water sensitive receiver(s)	<ul style="list-style-type: none"> • If exceedance is found to be caused by the reclamation activities, repeat in-situ measurement to confirm findings; • Inform IC(E), AFCD, contractor and EPD; • Check monitoring data, all plant, equipment and Contractor's working methods; • Discuss mitigation measures with IC(E), ER and Contractor; • Ensure mitigation measures are implemented; • Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days; • If exceedance occurs at WSD salt water intake, inform WSD. 	<ul style="list-style-type: none"> • Assess the effectiveness of the implemented mitigation measures. 	<ul style="list-style-type: none"> • Make agreement on the mitigation measures to be implemented; • Assess the effectiveness of the implemented mitigation measures; • Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. 	<ul style="list-style-type: none"> • Check all plant and equipment and consider changes of working methods; • Discuss with ET, IC(E) and ER and submit proposal of mitigation measures to IC(E) and ER within 3 working days of notification; • Implement the agreed mitigation measures; • As directed by the Engineer, to slow down or to stop all or part of the construction activities.

Limit Levels and Action Plan for Landfill Gas

Parameter	Limit Level	Action
Oxygen	<19%	<ul style="list-style-type: none"> • Ventilate to restore oxygen to >19%
	<18%	<ul style="list-style-type: none"> • Stop works • Evacuate personnel/prohibit entry • Increase ventilation to restore oxygen to >19%
Methane	>10% LEL (i.e. > 0.5% by volume)	<ul style="list-style-type: none"> • Prohibit hot works • Ventilate to restore methane to <10% LEL
	>20% LEL (i.e. > 1% by volume)	<ul style="list-style-type: none"> • Stop works • Evacuate personnel / prohibit entry • Increase ventilation to restore methane to <10% LEL
Carbon Dioxide	>0.5%	<ul style="list-style-type: none"> • Ventilate to restore carbon dioxide to < 0.5%
	>1.5%	<ul style="list-style-type: none"> • Stop works • Evacuate personnel / prohibit entry • Increase ventilation to restore carbon dioxide to < 0.5%

Event and Action Plan for Coral Post-Translocation Monitoring

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level Exceedance	1. Check monitoring data; 2. Inform the IEC, ER and Contractor of the findings; 3. Increase the monitoring to at least once a month to confirm findings; 4. Propose mitigation measures for consideration	1. Discuss monitoring with the ET and the Contractor; 2. Review proposals for additional Monitoring and any other measures submitted by the Contractor and advise the ER accordingly.	1. Discuss with the IEC additional monitoring requirements and any other measures proposed by the ET; 2. Make agreement on the measures to be implemented.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the ER; 3. Implement the agreed measures.
Limit Level Exceedance	Undertake Steps 1-4 as in the Action Level Exceedance. If further exceedance of Limit Level, suspend construction works until an effective solution is identified.	1. Discuss monitoring with the ET and the Contractor; 2. Review proposals for additional Monitoring and any other measures submitted by the Contractor and advise the ER accordingly.	1. Discuss with the IEC additional monitoring requirements and any other measures proposed by the ET; 2. Make agreement on the measures to be implemented.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the ER; 3. Implement the agreed measures.

Mitigation Measures for Vibration Monitoring

Level	Contingency Action
Alert Level	<ul style="list-style-type: none"> ● The Engineer shall be informed immediately. ● The Contractor shall submit an investigation report to describe works being undertaken. To review the instrument responses and to study the cause of undue response. ● The Contractor shall review and increase the instrumentation monitoring and reporting frequency, if applicable. ● The Contractor shall submit a detailed plan of action describing the measures to be taken should the concerned instrument reach the action level to the Engineer for approval.
Alarm Level	<ul style="list-style-type: none"> ● The Engineer shall be informed immediately. ● The active construction works may require to be suspended subject to the Engineer's review of monitoring data. ● The Contractor shall immediately implement the measures as defined in the detailed plan of action to prevent further ground movement and groundwater drawdown etc. ● The Contractor shall prepare a detailed investigation report to study the cause of the exceedance ● The Contractor shall propose a contingency plan for the Engineer's approval in the event that alarm value is reached or exceeded ● The Contractor shall develop an emergency plan for the Engineer's approval in the event the applied contingency measures cannot control the situation. ● The Contractor shall meet the Engineer to discuss the instrument response and review the effectiveness of the implemented measures. ● The Contractor shall carry out design review of the works

Action Level	<ul style="list-style-type: none">● Consideration shall be given to suspend all active construction works and the Engineer shall be informed immediately● The Contractor shall immediately implement the measures defined in the contingency plan● The Contractor shall implement the measures defined in the emergency plan in the event that the applied contingency measures are found inadequate● The Contractor shall provide a complete report to examine the construction method and review the response of the instruments with full history of the monitoring data and construction activities and necessary design update● To resume the suspended activities, the Contractor shall demonstrate to the Engineer's satisfaction that it is safe to do so with approval from the Engineer.
--------------	--

**APPENDIX N
ENVIRONMENTAL MITIGATION
IMPLEMENTATION SCHEDULE (EMIS)**

Table I – Recommended Mitigation Measures stipulated in EM&A Manual of the Project

(Further information on observations/reminders/non-compliance made during site audit should refer to Table II)

- Key:**
- ^ Mitigation measure was fully implemented.
 - * Observation/reminder was made during site audit but improved/rectified by the contractor.
 - # Observation/reminder was made during site audit but not yet improved/rectified by the contractor.
 - X Non-compliance of mitigation measure
 - Non-compliance but rectified by the contractor
 - N/A Not Applicable

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
Air Quality Impact								
S3.8.1	Watering eight times a day on active works areas, exposed areas and paved haul roads	To minimize the dust impact	Contractor	All Active Work Sites	Construction phase	APCO	*(1)/#(1)	3.12
S3.8.1	Enclosing the unloading process at barging point by a 3-sided screen with top tipping hall, provision of water spraying and flexible dust curtains	To minimize the dust impact	Contractor	Barging Points	Construction phase	APCO	^	3.12
S3.8.7	Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices: <ul style="list-style-type: none"> - Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. - Use of frequent watering for particularly dusty construction areas and areas close to ASRs. - Side enclosure and covering of any aggregate or dusty material storage piles to 	To minimize the dust impact	Contractor	All Construction Work Sites	Construction phase	APCO and Air Pollution Control (Construction Dust) Regulation	*(1)/#(1) *(1)/#(1)	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<p>reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.</p> <ul style="list-style-type: none"> - Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. - Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations. - Establishment and use of vehicle wheel and body washing facilities at the exit points of the site. - Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading area of barging point, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods. - Provision of not less than 2.4m high hoarding from ground level along site boundary where adjoins a road, streets or other accessible to the public except for a site entrance or exit. - Imposition of speed controls for vehicles on site haul roads. - Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs - Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides. - Instigation of an environmental monitoring and auditing program to monitor the 						<p>*(1)/#(1)</p> <p>^</p> <p>N/A</p> <p>*(1)/#(1)</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p>	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	construction process in order to enforce controls and modify method of work if dusty conditions arise.							
/	Emission from Vehicles and Plants <ul style="list-style-type: none"> • All vehicles shall be shut down in intermittent use. • Only well-maintained plant should be operated on-site and plant should be serviced regularly to avoid emission of black smoke. • All diesel fuelled construction plant within the works areas shall be powered by ultra low sulphur diesel fuel (ULSD) 	Reduce air pollution emission from construction vehicles and plants	Contractor	All construction sites	Construction stage	• APCO	^ ^ ^	
/	Valid No-road Mobile Machinery (NRMM) labels should be provided to regulated machines	Reduce air pollution emission from construction vehicles and plants	Contractor	All construction sites	Construction stage	• APCO	*(2)/#(2)	
Noise Impact (Construction Phase)								
S4.8	- Use of quiet PME. Use of movable noise barriers for Excavator, Lorry, Dump Truck, Mobile Crane, Compactor, Concrete Mixer Truck, Concrete Lorry Mixer, Breaker, Mobile Crusher, Backhoe, Vibratory Poker, Saw, Asphalt Paver, Vibratory Roller, Vibrolance, Hydraulic Vibratory Lance and Piling (Vibration Hammer). Use of full enclosure for Air Compressor, Compressor, Bar Bender, Generator, Drilling Rig, Chisel, Large Diameter Bore Piling, Grout Mixer & Pump and Concrete Pump.	To minimize construction noise impact arising from the Project at the affected NSRs	Contractor	Work Sites	Construction phase	EIAO-TM, NCO	N/A	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
Noise Mitigation Plan	Use of Temporary Noise Barriers or Full Enclosure for PME according to the approved Noise Mitigation Plan	To minimize construction noise impact arising from the Project at the affected NSRs	Contractor	Work Sites	Construction phase	EIAO-TM, NCO	*(3)/#(3)	
S4.9	<p>Good Site Practice</p> <ul style="list-style-type: none"> - Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program - Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program. - Mobile plant, if any, should be sited as far away from NSRs as possible. - Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum. - Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. - Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities. 	To minimize construction noise impact arising from the Project at the affected NSRs	Project Proponent	Work sites	Construction Period	EIAO-TM, NCO	^ ^ ^ ^ ^ ^	
S4.9	Scheduling of Construction Works during School Examination Period	To minimize construction noise impact arising from the	Contractor	Work site near school	Construction phase	EIAO-TM, NCO	N/A	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
		Project at the affected NSRs						
Water Quality Impact (Construction Phase)								
S5.6.24	The dry density of filling material for the TKO-LT Tunnel reclamation should be 1,900kg/m ³ , with fine content of 25% or less	Control potential impacts from filling activities	CEDD's Contractors	Work site	Construction Phase	EIAO-TM, WPCO	N/A	
S5.8.1	Non-dredged method by constructing steel cellular caisson structure with stone column shall be adopted for construction of seawall foundation. During the stone column installation (also including the installation of steel cellular caisson), silt curtain shall be employed around the active stone column installation points.	Control potential impacts from filling activities	CEDD's Contractors	Work site	Construction Phase	EIAO-TM, WPCO	N/A	3.2B
S5.8.2	Formation of seawall enclosing the reclamation for Road P2 (notwithstanding an opening of about 50m for marine access) shall be completed prior to the filling activities. The seawall opening of about 50m wide for marine access shall be selected at a location as indicatively shown in Appendix 5.10. No more than 3 filling barge trips per day shall be made with a maximum daily rate of 3,000m ³ (i.e. 1,000 m ³ per trip) for the filling operation at the reclamation area for Road P2. All filling works shall be carried out behind the seawall with the use of single silt curtain at the marine access.	Control potential impacts from filling activities	CEDD's Contractors	Work site	Construction Phase	EIAO-TM, WPCO	N/A	3.2C
S5.8.3	Other good site practices should be undertaken during filling operations include: - all marine works should adopt the environmental friendly construction methods as far as practically possible including the use of cofferdams to cover the construction area to separate the construction works from the sea;	Control potential impacts from filling activities and marine-	CEDD's Contractors	Work site	Construction Phase	EIAO-TM, WPCO, Waste Disposal Ordinance (WDO)	*(4)/#(4)	3.3C

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<ul style="list-style-type: none"> - floating single silt curtain shall be employed for all marine works; - all vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; - all hopper barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material; - excess material shall be cleaned from the decks and exposed fittings of barges before the vessel is moved; - adequate freeboard shall be maintained on barges to reduce the likelihood of decks being washed by wave action; - loading of barges and hoppers should be controlled to prevent splashing of filling material into the surrounding water. Barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation; - any pipe leakages shall be repaired quickly. Plant should not be operated with leaking pipes; - construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site or dumping grounds; and - before commencement of the reclamation works, the holder of Environmental Permit has to submit plans showing the phased construction of the reclamation, design and operation of the silt curtain. 	<p>based construction</p>					<p>*(4)/#(4) ^ ^ ^ ^ ^ ^ ^</p>	<p>2.8</p>

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
S5.8.4	Site specific mitigation plan for reclamation areas using public fill materials should be submitted for EPD agreement before commencement of construction phase with due consideration of good site practices.	Control potential impacts from filling activities and marine based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	N/A	
ERR S5.6.1	<p>To minimize water quality impact arising from the dredging and filling works for Reclamation for Road P2, the following mitigation measures shall be implemented:</p> <ul style="list-style-type: none"> - Before carrying out any dredging and underwater filling works, a temporary barrier shall first be constructed to a height above the high water mark to completely enclose the works site (without any opening at the barrier wall) - The temporary barrier fully enclosing the dredging and underwater filling works site shall not be removed before completion of all dredging and underwater filling works. - Water quality sampling and testing shall be carried out to demonstrate that the water quality inside the enclosed barrier is comparable to the ambient or baseline levels prior to the removal of the fully enclosed barrier. - Silt curtains shall be deployed for the installation and removal of the temporary barrier and at the double water gates marine access opening during its operation. The general of arrangement of silt curtain is shown in Figure 7 of the existing Environmental Permit (No. EP-458/2013/C). 	Control potential impacts from dredging and filling works for Reclamation for Road P2	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^ ^ N/A ^	3.3E

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
S5.8.5	It is important that appropriate measures are implemented to control runoff and drainage and prevent high loading of SS from entering the marine environment. Proper site management is essential to minimise surface water runoff, soil erosion and sewage effluents.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.6	Any practical options for the diversion and realignment of drainage should comply with both engineering and environmental requirements in order to ensure adequate hydraulic capacity of all drains.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Design Stage and Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO, TM-DSS	^	
S5.8.7	Construction site runoff and drainage should be prevented or minimised in accordance with the guidelines stipulated in the EPD's Practice Note for Professional Persons, Construction Site Drainage (ProPECC PN 1/94). Good housekeeping and stormwater best management practices, as detailed in below, should be implemented to ensure that all construction runoff complies with WPCO standards and no unacceptable impact on the WSRs arises due to construction of the TKO-LT Tunnel. All discharges from the construction site should be controlled to comply with the standards for effluents discharged into the corresponding WCZ under the TM-DSS.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO, TM-DSS	#(5)	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
S5.8.8	Exposed soil areas should be minimised to reduce the potential for increased siltation, contamination of runoff, and erosion. Construction runoff related impacts associated with the above ground construction activities can be readily controlled through the use of appropriate mitigation measures which include: - use of sediment traps; and - adequate maintenance of drainage systems to prevent flooding and overflow.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	N/A ^	
S5.8.9	Construction site should be provided with adequately designed perimeter channel and pretreatment facilities and proper maintenance. The boundaries of critical areas of earthworks should be marked and surrounded by dykes or embankments for flood protection. Temporary ditches should be provided to facilitate runoff discharge into the appropriate watercourses, via a silt retention pond. Permanent drainage channels should incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.10	Ideally, construction works should be programmed to minimise surface excavation works during the rainy season (April to September). All exposed earth areas should be completed as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
S5.8.11	Sedimentation tanks of sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8m ³ capacity, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity is flexible and able to handle multiple inputs from a variety of sources and particularly suited to applications where the influent is pumped.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO S5	#(6)	
S5.8.12	Earthworks final surfaces should be well compacted and the subsequent permanent work or surface protection should be carried out immediately after the final surfaces are formed to prevent erosion caused by rainstorms. Appropriate drainage like intercepting channels should be provided where necessary.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO S5	^	
S5.8.13	Measures should be taken to minimize the ingress of rainwater into trenches. If excavation of trenches in wet seasons is necessary, they should be dug and backfilled in short sections. Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO S5	^	
S5.8.14	Open stockpiles of construction materials (for examples, aggregates, sand and fill material) of more than 50m ³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.	Control potential impacts from construction site runoff and land-	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
		based construction						
S5.8.15	Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers. Discharge of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.16	Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecast, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.17	Oil interceptors should be provided in the drainage system and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	N/A	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES
April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
S5.8.18	All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and located wheel washing bay should be provided at every site exit, and washwater should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheelwash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.19	Silt removal facilities, channels and manholes should be maintained and the deposited silt and grit should be removed regularly, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.20	It is recommended that on-site drainage system should be installed prior to the commencement of other construction activities. Sediment traps should be installed in order to minimise the sediment loading of the effluent prior to discharge into foul sewers. There shall be no direct discharge of effluent from the site into the sea.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES
April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
S5.8.21	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment control measures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage should be reinstated to its original condition when the construction work has finished or the temporary diversion is no longer required.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.22	All fuel tanks and storage areas should be provided with locks and be located on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank, to prevent spilled fuel oils from reaching the coastal waters.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.23	Minimum distances of 100m shall be maintained between the existing or planned stormwater discharges and the existing or planned seawater intakes during construction and operational phases	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	EIAO-TM, WPCO, TMDSS	^	
S5.8.24	Under normal circumstances, groundwater pumped out of wells, etc. for the lowering of ground water level in basement or foundation construction, and groundwater seepage pumped out of tunnels or caverns under construction should be discharged into storm drains after the removal of silt in silt removal facilities.	Control potential impacts from construction site runoff and land-	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
		based construction						
S5.8.25 - S5.8.27 & Table 5.18	Grouting would be adopted as measure to reduce the groundwater inflow into the tunnel. During the tunnel excavation, the inflow rate of groundwater into the tunnel will be measured during the excavation. The groundwater levels above the tunnel will also be monitored by piezometers. If the inflow rate exceeds the pre-determined groundwater control criteria or the groundwater drawdown exceeds the required limit, pre-excavation grouting will be required to reduce the groundwater inflow. No significant change of groundwater levels would therefore be expected. Any chemicals/foaming agents which would be entrained to the groundwater should be biodegradable and non-toxic throughout the tunnel construction. Potential groundwater quality impact would be minimal as the used material is non-toxic and biodegradable. No adverse groundwater quality would therefore be expected. Prescriptive measures in the form of an Action Plan with pre-emptive and re-active to preserve the groundwater levels at all times during the tunnel construction are set out in Table 5.18.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO, Buildings Ordinance	N/A	
S5.8.28	Water used in ground boring and drilling for site investigation or rock / soil anchoring should as far as practicable be recirculated after sedimentation. When there is a need for final disposal, the wastewater should be discharged into storm drains via silt removal facilities.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Design Stage and Construction Phas	ProPECC PN 1/94, EIAOTM, WPCO	N/A	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
S5.8.29 - S5.8.31	Wastewater generated from the washing down of mixing trucks and drum mixers and similar equipment should whenever practicable be recycled. The discharge of wastewater should be kept to a minimum. To prevent pollution from wastewater overflow, the pump sump of any water recycling system should be provided with an online standby pump of adequate capacity and with automatic alternating devices. Under normal circumstances, surplus wastewater may be discharged into foul sewers after treatment in silt removal and pH adjustment facilities (to within the pH range of 6 to 10). Disposal of wastewater into storm drains will require more elaborate treatment.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.32	All vehicles and plant should be cleaned before they leave a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. A wheel washing bay should be provided at every site exit if practicable and wash-water should have sand and silt settled out or removed before discharging into storm drains. The section of construction road between the wheel washing bay and the public road should be paved with backfall to reduce vehicle tracking of soil and to prevent site runoff from entering public road drains.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.33	Bentonite slurries used in diaphragm wall and borepile construction should be reconditioned and reused wherever practicable. If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	N/A	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
S5.8.34	If the used bentonite slurry is intended to be disposed of through the public drainage system, it should be treated to the respective effluent standards applicable to foul sewer, storm drains or the receiving waters as set out in the WPCO Technical Memorandum on Effluent Standards.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	N/A	
S5.8.35	Water used in water testing to check leakage of structures and pipes should be reused for other purposes as far as practicable. Surplus unpolluted water could be discharged into storm drains.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	N/A	
S5.8.36	Sterilization is commonly accomplished by chlorination. Specific advice from EPD should be sought during the design stage of the works with regard to the disposal of the sterilizing water. The sterilizing water should be reused wherever practicable.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Design Stage and Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	N/A	
S5.8.37	Before commencing any demolition works, all sewer and drainage connections should be sealed to prevent building debris, soil, sand etc. from entering public sewers/drains.	Control potential impacts from construction site runoff and land-	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	N/A	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
		based construction						
S5.8.38	Wastewater generated from building construction activities including concreting, plastering, internal decoration, cleaning of works and similar activities should not be discharged into the stormwater drainage system. If the wastewater is to be discharged into foul sewers, it should undergo the removal of settleable solids in a silt removal facility, and pH adjustment as necessary	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.39	Acidic wastewater generated from acid cleaning, etching, pickling and similar activities should be neutralized to within the pH range of 6 to 10 before discharging into foul sewers. If there is no public foul sewer in the vicinity, the neutralized wastewater should be tinkered off site for disposal into foul sewers or treated to a standard acceptable to storm drains and the receiving waters	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.40	Wastewater collected from canteen kitchens, including that from basins, sinks and floor drains, should be discharged into foul sewer via grease traps capable of providing at least 20 minutes retention during peak flow.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	N/A	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
S5.8.41	Drainage serving an open oil filling point should be connected to storm drains via a petrol interceptor with peak storm bypass.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.42	Vehicle and plant servicing areas, vehicle wash bays and lubrication bays should as far as possible be located within roofed areas. The drainage in these covered areas should be connected to foul sewers via a petrol interceptor. Oil leakage or spillage should be contained and cleaned up immediately. Waste oil should be collected and stored for recycling or disposal in accordance with the Waste Disposal Ordinance.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	*(7)/#(7)	
S5.8.43	Construction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage may need to be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor shall also be responsible for waste disposal and maintenance practices.	Control potential impacts from construction site runoff and land-based construction	CEDD's Contractors	Work site	Construction Phase	ProPECC PN 1/94, EIAOTM, WPCO	^	
S5.8.44	Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste)	Control potential impacts from accidental	CEDD's Contractors	Work site	Construction Phase	EIAO-TM, WPCO, WDO	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	(General) Regulation should be observed and complied with for control of chemical wastes.	spillage of chemicals						
S5.8.45	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	Control potential impacts from accidental spillage of chemicals	CEDD's Contractors	Work site	Construction Phase	EIAO-TM, WPCO	*(8)	
S5.8.46	Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The "Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes" published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows: <ul style="list-style-type: none"> - suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport; - chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents; and - storage area should be selected at a safe location on site and adequate space should be allocated to the storage area. 	Control potential impacts from accidental spillage of chemicals	CEDD's Contractors	Work site	Construction Phase	EIAO-TM, WPCO, WDO	^ ^ ^	
S5.8.47	Collection and removal of floating refuse should be performed at regular intervals on a daily basis. The contractor should be responsible for keeping the water within the site boundary and the neighbouring water free from rubbish.	Control potential impacts from floating refuse and debris	CEDD's Contractors	Work site	Construction Phase	EIAO-TM, WPCO,	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
<i>Ecological Impact</i>								
S6.8.4	<p><i>Measures to Minimize Disturbance</i></p> <ul style="list-style-type: none"> - Use of Quiet Mechanical Plant during the construction phase should be adopted wherever possible. - Hoarding or fencing should be erected around the works area boundaries during the construction phase. The hoarding would screen adjacent habitats from construction phase activities, reduce noise disturbance to these habitats and also to restrict access to habitats adjacent to works areas by site workers; - Regular spraying of haul roads to minimize impacts of dust deposition on adjacent vegetation and habitats during the construction activities 	Minimize noise, human and traffic disturbance to terrestrial habitat and wildlife; and reduce dust generation	Design Team / Contractor	Land-based works are	Construction Phase	N/A	^ ^ ^	
S6.8.5	<p><i>Standard Good Site Practice</i></p> <ul style="list-style-type: none"> - Placement of equipment or stockpile in designated works areas and access routes selected on existing disturbed land to minimise disturbance to natural habitats. - Construction activities should be restricted to works areas that should be clearly demarcated. The works areas should be reinstated after completion of the works. - Waste skips should be provided to collect general refuse and construction wastes. The wastes should be properly disposed off-site in a timely manner. - General drainage arrangements should include sediment and oil traps to collect and control construction site run-off. - Open burning on works sites is illegal, and should be strictly prohibited. - Measures should also be put into place so that litter, fuel and solvents do not enter 	Reduce disturbance to surrounding habitats	Contractor	Land-based works are	Construction Phase	N/A	^ ^ ^ ^ ^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	the nearby watercourses.							
S6.8.6	<p><i>Measure to Minimize Groundwater Inflow</i></p> <ul style="list-style-type: none"> - The drained tunnel construction method with groundwater inflow control measures would generally be adopted. - During the tunnel excavation, pre-excavation grouting could be adopted to reduce the groundwater inflow and ensure that the tunnel would meet the long term water tightness requirements. 	Minimize groundwater inflow	Contractor	Tunnel	Construction Phase	N/A	N/A	N/A
S6.8.8	<p><i>Measure to Minimize Impact on Corals</i></p> <p><u>Coral translocation</u></p> <ul style="list-style-type: none"> - It is recommended to translocate the affected coral colonies, except the locally common <i>Oulastrea crispata</i>, within the reclamation area and bridge footprint to the other suitable locations as far as practicable. - The coral translocation should be conducted during the winter months (November-March) in order to avoid disturbance during their spawning period (i.e. July to October). - A detailed coral translocation plan with a description on the methodology for pretranslocation coral survey, translocation methodology, identification/proposal of coral recipient site, monitoring methodology for posttranslocation should be prepared during the detailed design stage. 	Minimize loss of coral	Design team, contractor, project operator	Within reclamation areas and pier footprint	Prior construction	N/A	^ ^ ^ ^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<ul style="list-style-type: none"> - The coral translocation plan should be subject to approval by relevant authorities (e.g. EPD and AFCD) before commencement of the coral translocation. All the translocation exercises should be conducted by experienced marine ecologist(s) who is/are approved by AFCD prior to commencement of coral translocation. <p><u>Post translocation Monitoring</u></p> <ul style="list-style-type: none"> - A coral monitoring programme is recommended to assess any adverse and unacceptable impacts to the translocated coral communities - Information gathered during each posttranslocation monitoring survey should include observations on the presence, survival, health condition and growth of the translocated coral colonies. These parameters should then be compared with the baseline results collected from the pre-translocation survey. 						<p style="text-align: center;">^</p> <p style="text-align: center;">^</p>	
<p>S6.8.9</p> <p>S6.8.10</p>	<p><i>Measure to Control Water Quality Impact</i></p> <ul style="list-style-type: none"> - Deployment of silt curtains around the active stone column installation points, opening of newly installed seawall and marine works area. - Diverting of the site runoff to silt trap facilities before discharging into storm drain; - Proper waste and dumping management; and - Standard good-site practice for land-based construction. 	<p>Control water quality impact, especially on suspended solid level; minimize the contamination of wastewater discharge, accidental chemical</p>	<p>Design Team, contractor</p>	<p>Marine and landbased works area</p>	<p>Construction phase</p>	<p>WQO</p>	<p>N/A</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p>	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
		spillage and construction site runoff to the receiving water bodies						
S6.8.11	<p>Compensation for Vegetation Loss</p> <ul style="list-style-type: none"> - Felling of mature trees should be compensated by planting of standard or heavy standard trees within or in vicinity of the affected area as far as practicable. Such compensatory planting for trees should be provided with at least a 1:1 ratio. In addition, vegetation at the temporarily affected area should be reinstated with species similar to the existing condition. 	Compensate for the vegetation loss	Design Team, contractor	Land-based works area	Construction phase	N/A	^	
Fisheries Impact								
S7.7.3	<p>Measure to Control Water Quality Impact</p> <ul style="list-style-type: none"> - Deployment of silt curtains around the active stone column installation points, opening of newly installed seawall and marine works area. 	Control water quality impact, especially on suspended solid level	Design Team / Contractor	Marine work area	Construction phase	WQO	^	
Waste Management (Construction Phase)								
S8.6.3	<p>Good Site Practices and Waste Reduction Measures</p> <ul style="list-style-type: none"> - Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; 	To reduce waste management impacts	Contractor	All work sites	Construction Phase	Waste Disposal Ordinance (Cap. 354)	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<ul style="list-style-type: none"> - Training of site personnel in site cleanliness, proper waste management and chemical handling procedures; - Provision of sufficient waste disposal points and regular collection of waste; - Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; and - Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. 					Land (Miscellaneous Provisions) Ordinance (Cap. 28)	^ ^ ^ *(9)	
S8.6.4	<p><i>Good Site Practices and Waste Reduction Measures (con't)</i></p> <ul style="list-style-type: none"> - Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; - Encourage collection of aluminium cans by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the workforce; - Proper storage and site practices to minimize the potential for damage or contamination of construction materials; and - Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste. 	To achieve waste reduction	Contractor	All work sites	Construction Phase	Waste Disposal Ordinance (Cap. 354) Land (Miscellaneous Provisions) Ordinance (Cap. 28)	^ ^ ^ ^	
S8.6.5	<p><i>Good Site Practices and Waste Reduction Measures (con't)</i></p> <p>The Contractor shall prepare and implement a WMP as part of the EMP in accordance with ETWB TCW No. 19/2005 which describes the arrangements for</p>	To achieve waste reduction	Contractor	All work sites	Construction Phase	ETWB TCW No. 19/2005	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<p>avoidance, reuse, recovery, recycling, storage, collection, treatment and disposal of different categories of waste to be generated from the construction activities. Such a management plan should incorporate site specific factors, such as the designation of areas for segregation and temporary storage of reusable and recyclable materials.</p> <p>The EMP should be submitted to the Engineer for approval. The Contractor should implement the waste management practices in the EMP throughout the construction stage of the Project. The EMP should be reviewed regularly and updated by the Contractor.</p>							
S8.6.6	<p><i>Good Site Practices and Waste Reduction Measures (con't)</i></p> <ul style="list-style-type: none"> - C&D materials would be reused in the project and other local concurrent projects as far as possible. 	To achieve waste reduction	Contractor	All work sites	Construction Phase	ETWB TCW No. 19/2005	^	
S8.6.7	<p><i>Storage, Collection and Transportation of Waste</i></p> <p>Should any temporary storage or stockpiling of waste is required, recommendations to minimize the impacts include:</p> <ul style="list-style-type: none"> - Waste, such as soil, should be handled and stored well to ensure secure containment, thus minimizing the potential of pollution; - Maintain and clean storage areas routinely; - Stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; and - Different locations should be designated to stockpile each material to enhance reuse. 	To minimize potential adverse environmental impacts arising from waste storage	Contractor	All work sites	Construction Phase	-	^ ^ ^ ^	
S8.6.8	<p><i>Storage, Collection and Transportation of Waste (con't)</i></p>	To minimize	Contractor	All work	Construction			

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<ul style="list-style-type: none"> - Remove waste in timely manner; - Waste collectors should only collect wastes prescribed by their permits; - Impacts during transportation, such as dust and odour, should be mitigated by the use of covered trucks or in enclosed containers; - Obtain relevant waste disposal permits from the appropriate authorities, in accordance with the Waste Disposal Ordinance (Cap. 354), Waste Disposal (Charges for Disposal of Construction Waste) Regulation (Cap. 345) and the Land (Miscellaneous Provisions) Ordinance (Cap. 28); - Waste should be disposed of at licensed waste disposal facilities; and - Maintain records of quantities of waste generated, recycled and disposed. 	potential adverse environmental impacts arising from waste collection and disposal		sites	Phase		^ ^ ^ ^ ^ ^	
S8.6.9	<p><i>Storage, Collection and Transportation of Waste (con't)</i></p> <ul style="list-style-type: none"> - Implementation of trip ticket system with reference to DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials, to monitor disposal of waste and to control fly-tipping at PFRFs or landfills. A recording system for the amount of waste generated, recycled and disposed (including disposal sites) should be proposed. 	To minimize potential adverse environmental impacts arising from waste collection and disposal	Contractor	All work sites	Construction Phase	DEVB TCW No. 6/2010	^	
S8.6.11 - S8.6.13	<p><i>Sorting of C&D Materials</i></p> <ul style="list-style-type: none"> - Sorting to be performed to recover the inert materials, reusable and recyclable materials before disposal off-site. - Specific areas shall be provided by the Contractors for sorting and to provide 	To minimize potential adverse environmental	Contractor	All work sites	Construction Phase	DEVB TCW No. 6/2010 ETWB TCW No.	^ ^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<p>temporary storage areas for the sorted materials.</p> <ul style="list-style-type: none"> - The C&D materials should at least be segregated into inert and non-inert materials, in which the inert portion could be reused and recycled in the reclamation as far as practicable before delivery to PFRFs. While opportunities for reusing the non-inert portion should be investigated before disposal of at designated landfills 					<p>33/2002</p> <p>ETWB TCW No. 19/2005</p>	^	
<p>S8.6.15 – S8.6.16</p>	<p>Sediments</p> <ul style="list-style-type: none"> - Sediment encountered may be reused as filling material on-site after cement stabilization. Cement-stabilization process is undertaken by mixing sediment and cement and will convert sediment to earth filling material. The treated sediment has to comply with Risk-Based Remediation Goals (RBRGs) before being reused in order not to raise any land contamination issue. The adoption of RBRGs to assess stabilized sediment has been proposed in the current C&DMMP. MFC has no adverse comment on the current C&DMMP. The sediment quality indicates that all sediments comply with most stringent RBRGs except for one sediment sample (TKO-EBH501 3-3.95m) with lead exceeding the RBRG. Except for the sediment sample (TKO-EBH501 3-3.95m), the chemical screening results do not indicate sediment as contaminated soil. It is anticipated that reuse of sediment except sediment sample (TKO-EBH501 3-3.95m) will not lead to land contamination. - Despite exceedance of RBRG, onsite reuse of sediment under sample (TKO-EBH501 33.95m) as filling material after cement stabilization is also a suitable 	<p>To ensure the sediment to be disposed of in an authorized and least impacted way</p>	<p>contractor</p>	<p>All works areas with sediments concern</p>	<p>Construction Phase</p>	<p>RBRG</p>	<p>N/A</p> <p>N/A</p>	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<p>treatment. Sediment quality indicates the sediment sample (TKO-EBH501 3-3.95m) exceed RBRG for lead. While cement stabilization will immobilize metal contaminants, it is capable to treat the exceedance on lead. The stabilized material should comply with UTS of Lead and UCS. If the treated material do not comply with UTS or UCS, re-stabilization have to be undertaken to meet compliance of UTS and UCS before reusing the treated sediment as filling material. However, further agreement on final disposal/treatment on sediment under sample (TKO-EBH501 3-3.95m) has to be sought from DEP</p>							
<p>S8.6.17 – S8.6.20</p>	<p>Sediments (con't)</p> <ul style="list-style-type: none"> - Requirements of the Air Pollution Control (Construction Dust) Regulation, where relevant, shall be adhered to during boring, excavation, transportation and disposal of sediments or cement stabilization of sediment. - A treatment area should be confined for carrying out the cement stabilization mixing and temporary stockpile. The area should be designed to prevent leachate from entering the ground. Leachate, if any, should be collected and discharged according to the Water Pollution Control Ordinance (WPCO). - In order to minimise the potential odour / dust emissions during boring, excavation and transportation of the sediment, the excavated sediments should be kept wet during excavation/boring and should be properly covered when placed on barges/trucks. Loading of the excavated sediment to the barge should be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding water. 	<p>To determine the best handling and treatment of sediment</p>	<p>Contractor</p>	<p>All works areas with sediments concern</p>	<p>Construction Phase</p>		<p>N/A N/A N/A N/A</p>	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<ul style="list-style-type: none"> - In order to minimise the exposure to contaminated materials, workers should, when necessary, wear appropriate personal protective equipments (PPE) when handling contaminated sediments. Adequate washing and cleaning facilities should also be provided on site. 							
S8.6.21	<p>Sediments (con't)</p> <ul style="list-style-type: none"> - Alternatively, excavated sediment can be treated with marine disposal. The basic requirements and procedures for excavated sediment disposal specified under ETWB TC(W) No. 34/2002 shall be followed. MFC is responsible for the provision and management of disposal capacity and facilities for the excavated sediment, while the permit of marine dumping is required under the Dumping at Sea Ordinance and is the responsibility of the DEP. 	To ensure the sediment to be disposed of in an authorized and least impacted way	contractor	All works areas with sediments concern	Construction Phase	ETWB TC(W) No. 34/2002 & Dumping at Sea Ordinance	N/A	
S8.6.23	<p>Sediments (con't)</p> <ul style="list-style-type: none"> - For allocation of sediment disposal sites and application of marine dumping permit, separate SSTP has to be submitted to EPD for agreement under DASO. Additional site investigation, based on the SSTP, maybe carried out in order to confirm the disposal arrangements for the proposed sediments removal. A Sediment Quality Report (SQR) shall then be required for EPD agreement under DASO prior to the tendering of the construction contract, discussing in details the site investigation, testing results as well as the delineation of each of the categories of excavated materials and the corresponding types of disposal. 	To determine the best handling and disposal option of sediment	Contractor	All works areas with sediments concern	Construction Phase	ETWB TC(W) No. 34/2002 & Dumping at Sea Ordinance	N/A	
S8.6.24 - S8.6.28	<p>Sediments (con't)</p> <ul style="list-style-type: none"> - The excavated sediments is expected to be loaded onto the barge and 	To ensure handling of	Contractor	All works areas with	Construction Phase	ETWB TC(W) No. 34/2002 &	N/A	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<p>ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the DEP.</p> <ul style="list-style-type: none"> - In order to minimise the exposure to contaminated materials, workers should, when necessary, wear appropriate personal protective equipments (PPE) when handling contaminated sediments. Adequate washing and cleaning facilities should also be provided on site. - Another possible arrangement for Type 3 disposal is by geosynthetic containment. A geosynthetic containment method is a method whereby the sediments are sealed in geosynthetic containers and, at the disposal site, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping, thereby meeting the requirements for fully confined mud disposal. 						<p>N/A</p> <p>N/A</p>	
S8.6.26	<p>Chemical Wastes.</p> <ul style="list-style-type: none"> - If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, 	To ensure proper management of chemical waste	Contractor	All works sites	Construction Phase	Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes Waste Disposal (Chemical Waste) (General)	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the Chemical Waste Treatment Centre at Tsing Yi, or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.					Regulation		
S8.6.27	<p>General Refuse</p> <ul style="list-style-type: none"> - General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material. 	To ensure proper management of general refuse	Contractor	All works sites	Construction Phase	Public Health and Municipal Services Ordinance (Cap. 132)	^	
Impact on Cultural Heritage (Construction Phase)								
S9.6.4	<p>Dust and visual impacts</p> <ul style="list-style-type: none"> - Temporarily fenced off buffer zone with allowance for public access (minimum 1 m) should be provided; - The open yard in front of the temple should be kept as usual for annual Tin Hau festival; - Monitoring of vibration impacts should be conducted when the construction works are less than 100m from the temple. 	To prevent dust and visual impacts	Contractors	Work areas	Construction Phase	EIAO; GCHIA; AMO	^ ^ ^	
S9.6.4	<p>Indirect vibration impact</p> <ul style="list-style-type: none"> - Vibration level is suggest to be controlled within a peak particle velocity (ppv) limit of 5mm/s measured inside the historical buildings; - Monitoring of vibration should be carried out during construction phase. 	To prevent indirect vibration impact	Contractors	Work areas	Construction Phase	Vibration Limits on Heritage Buildings by CEDD; GCHIA; AMO.	^ ^	3.7 3.7

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<ul style="list-style-type: none"> - Tilting and settlement monitoring should will be applied on the Cha Kwo Ling Tin Hau Temple as well. - A proposal with details for the mitigation measures and monitoring of impacts on built heritage shall be submitted to AMO for comments before commencement of work. 						^	3.7
							^	3.7
<i>Landscape and Visual Impact (Construction Phase)</i>								
Table 10.8.1	CM1 - Construction area and contractor's temporary works areas to be minimised to avoid impacts on adjacent landscape.	Avoid impact on adjacent landscape areas	CEDD (via Contractor)	General	Construction planning and during construction period	N/A	^	
Table 10.8.1	CM2 - Reduction of construction period to practical minimum.	Minimise duration of impact	CEDD (via Contractor)	N/A	Construction planning	N/A	^	
Table 10.8.1	CM3 - Topsoil, where the soil material meets acceptable criteria and where practical, to be stripped and stored for re-use in the construction of the soft landscape works. The Contract Specification shall include storage and reuse of topsoil as appropriate.	To allow re-use of topsoil	CEDD (via Contractor)	General	Site clearance	As per the Particular Specification	^	
Table 10.8.1	CM4 - Existing trees at boundary of site and retained trees within site boundary to be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification, under which the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in	To minimize tree loss	CEDD (via Contractor)	As per approved Tree Removal Application(s)	Site clearance and throughout construction period	ETWB TC 3/2006 and as per tree protection measures in Particular	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES
April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage).)		Specification		
Table 10.8.1	CM5 - Trees unavoidably affected by the works shall be transplanted where practicable. Where possible, trees should be transplanted direct to permanent locations rather than temporary holding nurseries. A detailed tree transplanting specification shall be provided in the Contract Specification and sufficient time for preparation shall be allowed in the construction programme.	To maximize preservation of existing trees	CEDD (via Contractor)	As per approved Tree Removal Application(s)	Site clearance	ETWB TC 3/2006 and as per tree protection measures in Particular Specification	^	
Table 10.8.1	CM6 - Advance screen planting of fast growing tree and shrub species to noise barriers and hoardings. Trees shall be capable of reaching a height >10m within 10 years.	To maximize screening of the works	CEDD (via Contractor)	At Lam Tin Interchange and edge of Road P2 landscape deck, TKO	Beginning of construction period	N/A	^	
Table 10.8.1	CM7 - Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material	To reduce visual intrusion	CEDD (via Contractor)	General	Throughout construction period	As per Particular Specification	N/A	
Table 10.8.1	CM8 - Control of night-time lighting by hooding all lights and through minimisation of night working periods.	To reduce visual intrusion	CEDD (via Contractor)	General	Throughout construction period	N/A	^	
Table 10.8.1	CM9 - Screening of works areas with hoardings with appropriate colours compatible with the surrounding area	Reduction of visual intrusion	CEDD (via Contractor)	Project site Boundary	Excretion of site hoarding	N/A	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
Table 10.8.1	CM10 - Avoidance of excessive height and bulk of site buildings and structure	Reduction of visual intrusion and integration with environment	CEDD (via Contractor)	Built structures	Design and construction stage	N/A	^	
Table 10.8.1	CM11 - Limitation of run-off into freshwater streams, ponds and sea areas	Avoidance of contamination of water courses and water bodie	CEDD (via Contractor)	TKO reclamation, TKO tunnel portal, Cha Kwo Ling roadworks	Throughout construction period	N/A	^	
Table 10.8.1	CM12 - Minimise area of reclamation and design the edges sensitively to tie in with adjacent coastline characte	Minimise loss of Junk Bay and integration with existing coastlin	CEDD (via Contractor)	Temporary reclamation for barging points at TKO and Lam Tin and permanent reclamation for TKO Interchange	Construction planning and reclamation stages	N/A	N/A	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
				slip roads and Road P2				
Landfill Gas Hazard (Design and Construction Phase)								
S11.5.9	<p>A Safety Officer, trained in the use of gas detection equipment and landfill gas-related hazards, should be present on site throughout the groundworks phase. The Safety Officer should be provided with an intrinsically safe portable instrument, which is appropriately calibrated and able to measure the following gases in the ranges indicated below:</p> <p>Methane 0-100% LEL and 0100% v/v Carbon dioxide 0-100% Oxygen 0-21%</p>	Protect the workers from landfill gas hazards	Contractor	Project sites within the Sai Tso Wan Landfill Consultation Zone	Construction phase	EPD's Landfill Gas Hazard Assessment Guidance Note	^	
S11.5.10 S11.5.25	<p>Safety Measures</p> <ul style="list-style-type: none"> - For staff who work in, or have responsibility for "at risk" area, such as all excavation workers, supervisors and engineers working within the Consultation Zone, should receive appropriate training on working in areas susceptible to landfill gas, fire and explosion hazards. - An excavation procedure or code of practice to minimize landfill gas related risk should be devised and carried out. - No worker should be allowed to work alone at any time in or near to any excavation. At least one other worker should be available to assist with a 	Protect the workers from landfill gas hazards	Contractor	Project sites within the Sai Tso Wan Landfill Consultation Zone	Construction phase	EPD's Landfill Gas Hazard Assessment Guidance Note Labour Department's Code of Practice for Safety and Health at Work in	^ ^ ^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<p>rescue if needed.</p> <ul style="list-style-type: none"> - Smoking, naked flames and all other sources of ignition should be prohibited within 15m of any excavation or ground-level confined space. “No smoking” and “No naked flame” notices should be posted prominently on the construction site and, if necessary, special areas should be designed for smoking. - Welding, flame-cutting or other hot works should be confined to open areas at least 15m from any trench or excavation. - Welding, flame-cutting or other hot works may only be carried out in trenches or confined spaces when controlled by a “permit to work” procedure, properly authorized by the Safety Officer (or, in the case of small developments, other appropriately qualified person). - The permit to work procedure should set down clearly the requirements for continuous monitoring for methane, carbon dioxide and oxygen throughout the period during which the hot works are in progress. The procedure should also require the presence of an appropriately qualified person, in attendance outside the 'confined area', who should be responsible for reviewing the gas measurements as they are made, and who should have executive responsibility for suspending the work in the event of unacceptable or hazardous conditions. Only those workers who are appropriately trained and fully aware of the potentially hazardous conditions which may arise should be permitted to carry out hot works in confined areas. 					Confined Space	^ ^ ^ ^ ^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<ul style="list-style-type: none"> - Where there are any temporary site offices, or any other buildings located within the Sai Tso Wan Landfill Consultation Zone which have enclosed spaces with the capacity to accumulate landfill gas, then they should either be located in an area which has been proven to be free of landfill gas (by survey using portable gas detectors); or be raised clear of the ground by a minimum of 500mm. This aims to create a clear void under the structure which is ventilated by natural air movement such that emission of gas from the ground are mixed and diluted by air. - Any electrical equipment, such as motors and extension cords, should be intrinsically safe. During piping assembly or conduiting construction, all valves/seals should be closed immediately after installation. As construction progresses, all valves/seals should be closed to prevent the migration of gases through the pipeline/conduit. All piping /conduiting should be capped at the end of each working day. - During construction, adequate fire extinguishing equipment, fire-resistant clothing and breathing apparatus (BA) sets should be made available on site. - Fire drills should be organized at not less than six monthly intervals. - The contractor should formulate a health and safety policy, standards and instructions for site personnel to follow. - All personnel who work on the site and all visitors to the site should be made aware of the possibility of ignition of gas in the vicinity of excavations. Safety notices (in Chinese and English) should be posted at prominent position around 						<p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p> <p style="text-align: center;">^</p>	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<p>the site warning danger of the potential hazards.</p> <ul style="list-style-type: none"> - Service runs within the Consultation Zone should be designated as “special routes”; utilities companies should be informed of this and precautionary measures should be implemented. Precautionary measures should include ensuring that staff members are aware of the potential hazards of working in confined spaces such as manholes and service chambers, and that appropriate monitoring procedures are in place to prevent hazards due to asphyxiating atmospheres in confined spaces. Detailed guidance on entry into confined spaces is given in Code of Practice on Safety and Health at Work in Confined Spaces (Labour Department, Hong Kong). - Periodically during ground-works construction within the 250m Consultation Zone, the works area should be monitored for methane, carbon dioxide and oxygen using appropriately calibrated portable gas detection equipment. The monitoring frequency and areas to be monitored should be set down prior to commencement of ground-works either by the Safety Officer or an approved and appropriately qualified person. 						^	
S11.5.26 - S11.5.31	<p>Monitoring</p> <ul style="list-style-type: none"> ● Routine monitoring should be carried out in all excavations, manholes, chambers, relocation of monitoring wells and any other confined spaces that may have been created. All measurements in excavations should be made with the extended monitoring tube located not more than 10 mm from the exposed ground surface. Monitoring should be performed properly to make 	Protect the workers from landfill gas hazards	Contractor	Project sites within the Sai Tso Wan Landfill Consultation Zone	Construction phase	EPD’s Landfill Gas Hazard Assessment Guidance Note	^	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	<p>sure that the area is free of landfill gas before any man enters into the area.</p> <ul style="list-style-type: none"> ● For excavations deeper than 1m, measurements should be carried out: <ul style="list-style-type: none"> - at the ground surface before excavation commences;- - immediately before any worker enters the excavation; - at the beginning of each working day for the entire period the excavation remains open; and - periodically throughout the working day whilst workers are in the excavation. ● For excavations between 300mm and 1m deep, measurements should be carried out: <ul style="list-style-type: none"> - directly after the excavation has been completed; and - periodically whilst the excavation remains open. ● For excavations less than 300mm deep, monitoring may be omitted, at the discretion of the Safety Officer or other appropriately qualified person. ● Depending on the results of the measurements, actions required will vary and should be set down by the Safety Officer or other appropriately qualified person. ● The exact frequency of monitoring should be determined prior to the commencement of works, but should be at least once per day, and be carried out by a suitably qualified or qualified person before starting the work of the day. Measurements shall be recorded and kept as a record of safe working conditions with copies of the site diary and submitted to the Engineer for approval. The Contractor may elect to carry out monitoring via an automated 						<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p>	

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

EIA Ref.	Recommended Mitigation Measures	Objectives of the recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to Implement the measures?	What requirements or standards for the measures to achieve?	Status	E.P Condition
	monitoring system.							
S11.5.32	The hazards from landfill gas during the construction stage within the Sai Tso Wan Landfill Consultation Zone should be minimized by suitable precautionary measures recommended in Chapter 8 of the Landfill Gas Hazard Assessment Guidance Note.	construction stage within the Sai Tso Wan Protect the workers from landfill gas hazards	Contractor	Project sites within the Sai Tso Wan Landfill Consultation Zone	Construction phase	EPD's Landfill Gas Hazard Assessment Guidance Note	N/A	

Table II - Observations/reminders/non-compliance made during Site Audit

- Key:**
- * Observation/reminder was made during site audit but improved/rectified by the contractor.
 - # Observation/reminder was made during site audit but not yet improved/rectified by the contractor.
 - X Non-compliance of mitigation measure
 - Non-compliance but rectified by the contractor

Status / Remark	EIA Ref.	Recommended Mitigation Measures	Contract No.	Work Sites	Details of Observation/Reminder
Air Quality Impact					
* (1)	S3.8.1	Watering eight times a day on active works areas, exposed areas and paved haul roads	NE/2015/01	Construction of Lam Tin Interchange	Water spraying should be provided to slopes in LTI more frequently for dust suppression.
	S3.8.7	Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices: <ul style="list-style-type: none"> - Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. - Use of frequent watering for particularly dusty construction areas and areas close to ASRs. - Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading area of barging point, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods. - Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs. 	NE/2015/01	Construction of Lam Tin Interchange	Water spraying should be provided to slopes in LTI for dust suppression.
			NE/2015/02	Construction of Road P2	Haul road at Portion 4 was observed dry. The Contractor should provide sufficient water spraying for dust suppression.
			NE/2015/02	Construction of Road P2	The Contractor was reminded to repair the retractable tube of the drill rig in Portion 4 and ensure its integrity at all time.
# (1)			NE/2015/01	Construction of Lam Tin Interchange	Water sprinklers on Slope H should be provided to all breaking works for dust suppression.
			NE/2015/02	Construction of Road P2	The Contractor was reminded to provide water spraying for unloading / loading activity at Portion 5

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

Status / Remark	EIA Ref.	Recommended Mitigation Measures	Contract No.	Work Sites	Details of Observation/Reminder
			NE/2015/02	Construction of Road P2	The Contractor was reminded to lower the level of stockpiles in Work Area A and cover them with impervious sheet.
			NE/2017/02	Construction of Road P2/D4	Dusty materials should be removed to prevent dust generation.
/	/	Emission from Vehicles and Plants <ul style="list-style-type: none"> • Only well-maintained plant should be operated on-site and plant should be serviced regularly to avoid emission of black smoke. 	NE/2015/02	Construction of Road P2	The Contractor was reminded to maintain the construction vessels regularly to prevent black smoke emission.
* (2)	/	Valid No-road Mobile Machinery (NRMM) labels should be provided to regulated machines	NE/2015/01	Construction of TKO Portal	NRMM labels should be properly displayed on PMEs in Portion 6 in TKO site.
# (2)			NE/2015/02	Construction of Road P2	The Contractor was reminded to replace NRMM labels when needed.
Noise Impact (Construction Phase)					
* (3)	Noise Mitigation Plan	Use of Temporary Noise Barriers or Full Enclosure for PME according to the approved Noise Mitigation Plan	NE/2015/02	Construction of Road P2	The Contractor was reminded to properly erect noise barriers for the drill rig in Portion 7 to reduce noise nuisance to nearby NSR.
# (3)			NE/2015/02	Construction of Road P2	To place the acoustic box properly for breaking work in Portion 4.
# (3)			NE/2015/02	Construction of Road P2	The Contractor was reminded to erect an effective acoustic mat for the derrick barge at the unloading area in Portion 7 and properly erect the noise barrier near the entrance of Portion 7.
Water Quality Impact (Construction Phase)					
* (4)	S5.8.3	Other good site practices should be undertaken during filling operations include:	NE/2015/01	Construction of	Gaps between silt curtains in TKO site should be

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

Status / Remark	EIA Ref.	Recommended Mitigation Measures	Contract No.	Work Sites	Details of Observation/Reminder
# (4)		<ul style="list-style-type: none"> - all marine works should adopt the environmental friendly construction methods as far as practically possible including the use of cofferdams to cover the construction area to separate the construction works from the sea; - floating single silt curtain shall be employed for all marine works; 		TKO Portal	avoided.
			NE/2015/02	Construction of Road P2	Silt curtains near the double water gate are observed damaged. The Contractor should maintain the silt curtains properly and ensure the geotextile is extended to seabed.
			NE/2015/02	Construction of Road P2	To repair the damaged silt curtain at the double water gate and deploy silt curtains around the cofferdam properly without gaps.
			NE/2015/01	Construction of TKO Portal	Silt curtain near marine platform in TKO site should be maintained to prevent untreated discharge.
# (5)	S5.8.7	Construction site runoff and drainage should be prevented or minimised in accordance with the guidelines stipulated in the EPD's Practice Note for Professional Persons, Construction Site Drainage (ProPECC PN 1/94). Good housekeeping and stormwater best management practices, as detailed in below, should be implemented to ensure that all construction runoff complies with WPCO standards and no unacceptable impact on the WSRs arises due to construction of the TKO-LT Tunnel. All discharges from the construction site should be controlled to comply with the standards for effluents discharged into the corresponding WCZ under the TM-DSS.	NE/2015/02	Construction of Road P2	The Contractor was reminded to clear the sediment at the unloading area at Portion 7 regularly.
# (6)	S5.8.11	Sedimentation tanks of sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8m ³ capacity, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity is flexible and able to handle multiple inputs from a variety of sources and particularly suited to applications where the influent is pumped.	NE/2015/03	Construction of Northern Footbridge	Water leakage was found in the sedimentation tank in West Pier. The Contractor was reminded to rectify immediately and check the performance regularly

Ecological Impact

App N - IMPLEMENTATION SCHEDULE AND RECOMMENDED MITIGATION MEASURES

April 2018

Status / Remark	EIA Ref.	Recommended Mitigation Measures	Contract No.	Work Sites	Details of Observation/Reminder
* (7)	S 5.8.42	Vehicle and plant servicing areas, vehicle wash bays and lubrication bays should as far as possible be located within roofed areas. The drainage in these covered areas should be connected to foul sewers via a petrol interceptor. Oil leakage or spillage should be contained and cleaned up immediately. Waste oil should be collected and stored for recycling or disposal in accordance with the Waste Disposal Ordinance.	NE/2015/01	Construction of TKO Portal	PME in Portion 6 in TKO site should be maintained regularly to avoid oil leakage.
			NE/2015/02	Construction of Road P2	To clear the oil stain found under the pre-boring machine in Portion 5.
			NE/2015/02	Construction of Road P2	The Contractor was reminded to properly clear the oil stain at the double water gate and Portion 4.
# (7)					
* (8)	S5.8.45	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	NE/2015/01	Construction of Lam Tin Interchange	Drip tray should be provided to chemical containers in WA1.
Waste Management (Construction Phase)					
* (9)	S8.6.3	Good Site Practices and Waste Reduction Measures - Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.	NE/2017/02	Construction of Road P2/D4	General refuse should be collected and disposed regularly.

**APPENDIX O
SUMMARIES OF ENVIRONMENTAL
COMPLAINT, WARNING, SUMMON
AND NOTIFICATION OF SUCCESSFUL
PROSECUTION**

Appendix O - Cumulative Log for Complaints, Notifications of Summons and Successful Prosecutions

Cumulative Complaint Log for Tseung Kwan O - Lam Tin Tunnel

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
118	25 th January 2018	Not specified/ Construction of Lam Tin Interchange	Public	Air Quality	Conduction dust nuisance from works near Cha Kwo Ling Road and the complainant requested more wheel washing and water spray at Cha Kwo Ling Road near site entrance. (EPD Reference No.: K15/RE/00002751-18)	N	No specific dust generation works was carried out near Cha Kwo Ling Road. Water browser had been deployed for washing at junction between Cha Kwo Ling Road and site entrance to minimize dust impact to Cha Kwo Ling Road.	Closed
121	29 th January 2018	Not specified/ Construction of Lam Tin Interchange	Public	Air Quality	The complainant complained that a breaking operating in LTI near East Harbour Crossing Admin Building without water spray. (EPD Reference No.: K15/RE/00003007-16)	N	<p>According to the Engineer's site diaries, the major construction activities at the location of the complaint recorded included breaking works from 0800 hrs to 1800 hrs with 1 no. of backhoe with hydraulic breaker in operation on 29th January 2018. The breaking works near the location of the complaint is regarded to be the source of dust nuisance, thus the complaint is considered to be project related.</p> <p>The Contractor had implemented environmental mitigation measures in accordance with the "Implementation Schedule of Proposed Mitigation Measures" of EM&A Manual as below:</p> <ul style="list-style-type: none"> ● Breaking of rocks was provided with water spraying to reduce fugitive emission; and ● Hoarding with tarpaulin sheets were erected to further reduce dust generation due to breaking works. <p>With the above mitigation measures put in place, it is considered that construction dust impacts due to the construction of Lam Tin Interchange have been brought to a minimum.</p>	Closed

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
122	1 st , 9 th , 15 th February 2018	Not specified/ near Cha Kwo Ling Tsuen and Tin Hau Temple	Public	Air Quality	The complainant complained the dust nuisance on Cha Kwo Ling Road near Yau Tong and Tin Hau Temple.	N	<p>According to the information provided by the Contractor and confirmed by the Engineer of the Project, there were no construction activities in Portion 1 adjacent to Cha Kwo Ling Road during the time of complaint. Apart from the road traffic on Cha Kwo Ling Road, it is considered that the entering and leaving of construction vehicles from Portion 1 would also contribute to the dust and noise nuisance on Cha Kwo Ling Road.</p> <p>The Contractor had implemented environmental mitigation measures in accordance with the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual as follows:</p> <p><u>Air Quality:</u></p> <ul style="list-style-type: none"> ➤ Vehicle washing bay was set up at the site access of Portion 1 near Cha Kwo Ling Road (See Photo 1); ➤ The access road leading to and exiting from the wheel washing bay to Cha Kwo Ling Road was hard-paved to prevent vehicle tracking of soil and mud to public roads (See Photo 2); ➤ Water trucks and workers were dispatched to clear dust on Cha Kwo Ling Road and frequently perform water spraying to reduce dust generation due to vehicle movement (See Photo 3); ➤ Broken dust screen deployed in Cha Kwo Ling Barging Point was replaced (See Photo 4); <p><u>Noise:</u></p> <ul style="list-style-type: none"> ➤ Steel bridge with full enclosure was used by construction vehicles to access Cha Kwo Ling Barging Point to reduce noise nuisance generated by entering or leaving of dump trucks from Cha Kwo Ling Barging Point (See Photo 5). <p>The following recommendations were made to further enhance the mitigation measures:</p> <ul style="list-style-type: none"> ➤ To provide a hard-surfaced road between any cleaning facility and the public road ➤ To treat exposed earth by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen or other suitable surface stabilizer within six months after the last construction activity within the site; 	Closed
123	2 nd February 2018	Not specified/ near Cha Kwo Ling Tsuen	Public	Air Quality	Resident of Cha Kwo Ling Tsuen complained the dust nuisance on Cha Kwo Ling Road	N		
124	13 th February 2018	Not specified/ Construction of Lam Tin Interchange	Public	Air Quality	Resident of Cha Kwo Ling Tsuen complained the dust nuisance due to daytime open blasting and the broken dust curtain at Cha Kwo Ling Barging Point. (EPD Reference No.: K15/RE/00004536-18)	N		
125	14 th February 2018	Not specified/ near Cha Kwo Ling Tsuen	Public	Noise	Resident of Cha Kwo Ling Tsuen complained the noise of dump trucks and construction vehicles during night time	Y		

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
							<ul style="list-style-type: none"> ➤ To increase the frequency of cleaning Cha Kwo Ling by water trucks and workers to avoid the accumulation of dust on the public road; ➤ Where practicable, to provide sheltered area on the top and three sides for stockpiles of dusty materials, or perform frequent water spraying so as to maintain the entire surface wet; and ➤ To continue to properly implement noise mitigation measures as recommended in the Environmental Monitoring & Audit Manual and approved Noise Mitigation Plan; <p>The environmental conditions of the site and the control of works will be continuously reviewed and monitored by the Engineer and the Environmental Team.</p>	
126	21 st February 2018	19 th February 2018 / Construction of Road P2	Sai Kung District Council Member Mr. Chan Kai Wai	Noise	The complainant complained that barge was working in the marine works area in front of Ocean Shores from 7 am and emit loud noise.	Y	<p>According to the information provided and confirmed by the Engineer, no marine works were being conducted in Portion IX on 19 February 2018.</p> <p>The CCTV footage (provided by the Contractor, checked by Environmental Team and Independent Environmental Checker) confirms that no marine works were carried out from 7:00 to 10:00 am on 19 February 2018. Therefore, the complaint is considered non-Project related.</p> <p>For necessary PME operating during public holidays (including Sunday) on land-based works area, the Contractor is reminded to comply with the conditions of relevant CNPs and adopt good site practices recommended in the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual and the approved Noise Mitigation Plan of this Contract, including the following:</p> <ul style="list-style-type: none"> • Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program; • Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program; • Mobile plant, if any, should be sited as far away from NSRs as possible; 	Closed

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
							<ul style="list-style-type: none"> • Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum; • Plant known to emit noise strongly in one direction should, wherever possible be oriented so that the noise is directly away from the nearby NSRs; • Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities. <p>Furthermore, the Contractor had implemented environmental mitigation measures to minimize the noise nuisance from construction barges as follows:</p> <ul style="list-style-type: none"> • Maintenance of barge including lubrication of moving parts was performed to minimized noise from worn or loose parts; • Noise source on barge was covered with acoustic materials; <p>The environmental conditions of the site and the control of works will be continuously reviewed and monitored by the Engineer and the Environmental Team.</p>	
127	22 nd February 2018	Not specified/ Construction of Lam Tin Interchange	Public	Noise	The complainant complained the noise time construction noise from the site.	Y	Under Investigation	On-going
128 ⁽⁴⁾	3 rd March 2018	3 rd March 2018 / Construction of Lam Tin Interchange	Resident of Yau Lai Estate	Noise	The complainant complained the noise nuisance due to the breaking work at Lam Tin Interchange in the morning.	Y	Under Investigation	On-going
129 ⁽⁴⁾	3 rd March 2018	3 rd March 2018 / near Ocean Shore	Resident of Ocean Shore	Noise	The complainant complained the noise nuisance from the construction site near the Ocean Shore at 8:30am.	Y	According to the information provided and confirmed by the Engineer, one backhoe was deployed for site clearance on 3 March 2018. Major construction works were not yet commenced during the time of complaint but site clearance works in the morning. The excessive sound from movement of the poorly maintained backhoe is considered the	Closed

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
							<p>source of noise nuisance.</p> <p>The Contractor had implemented mitigation measures to prevent similar noise disturbance as follows:</p> <ul style="list-style-type: none"> • The use of concerned backhoe was stopped immediately by the Engineer upon receipt of the complaint. • Maintenance was provided to the concerned backhoe to avoid unnecessary disturbance. <p>The Engineer and the Environmental Team have reminded the Contractor to keep all powered mechanical equipment in good condition to minimize the noise impact from site clearance to nearby sensitive receiver.</p> <p>The following recommendations were made to further enhance the preventive measures:</p> <ul style="list-style-type: none"> • To maintain equipment in good condition to ensure quietest operation possible; • To repair any loosen and worn parts of the equipment, as soon as possible, to reduce excessive noise disturbance; • To schedule works carefully to avoid noisy works during sensitive hours; • To locate noisy equipment as far away as possible from any noise sensitive receivers; • To provide training to workers regularly on proper operation or appropriate use of equipment to avoid unnecessary noise impact. <p>The environmental conditions of the site and the control of works will be continuously reviewed and monitored by the Engineer and the Environmental Team.</p>	
130	6 th March 2018	Not specified/ Not specified	Anonymous	Air Quality	The complainant complained the dust nuisance from the	N	Under Investigation	On-going

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
					construction site and no water spraying system was observed near the construction site. He request to review the water sparing system more frequently			
131	7 th March 2018	Not specified / near Cha Kwo Ling Tsuen and Tin Hau Temple	Public	Air Quality	The complainant complained the dust nuisance on Cha Kwo Ling Road near Yau Tong and Tin Hau Temple. He request to perform frequent water spraying on Cha Kwo Ling Road.	N	Under Investigation	On-going
132	8 th March 2018	24 th February 2018 / Not specified	CEDD	Air Quality	The complainant complained that one dump truck left the site access being improperly / poorly covered	N	<p>According to checking by the Contractor of Contract No. NE/2015/02, it is noted that one dump truck left the site access being improperly / poorly covered. According to the CCTV Record at site entrance at Chi Shin Street, the vehicle left the site at 16:13 hrs on 24 February 2018. The record is shown in below CCTV captures.</p> <p>To improve performance by dump truck drivers, training has been provided by the Contractor to all staffs and dump truck drivers.</p> <p>Other than CCTV monitoring, the Contractor has deployed staff at the access to check the dump trucks to ensure that they are properly covered before leaving the site</p> <p>According to the weekly site inspection conducted by the Environmental Team on 13, 22 and 29 March 2018, no observation was identified regarding dump trucks leaving the site uncovered or poorly covered.</p> <p>The environmental condition of the site and control of works will be continuously reviewed and monitored by the Engineer and the Environmental Team.</p>	Closed
133	16 th March 2018	Not specified/ Construction of Lam Tin	Resident of Yung Lai House, Yau	Noise	The complainant complained the noisy breaking work at Lam Tin	Y	Under Investigation	On-going

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
	22 nd March 2018	Interchange	Lai Estate		Interchange at around 7pm. The complainant complained the noisy breaking work at Lam Tin Interchange after 7pm on 16 March 2018.			
134	19 th March 2018	Not specified / near Cha Kwo Ling Tsuen and Tin Hau Temple	Public	Air Quality	The complainant complained the dust nuisance from the construction site near Cha Kwo Ling Tsuen	N	Under Investigation	On-going
135	20 th March 2018	Not specified / near Cha Kwo Ling Road	茶果嶺居民關注組	Air Quality & Noise	The complainant complained about the dust nuisance near Cha Kwo Ling Road, construction noise at barging point at around 7am and blasting noise at Cha Kwo Ling site.	Y	Under Investigation	On-going
136	27 th March 2018	Not specified / near Po Shun Road	Anonymous	Noise	The complainant complained the noise nuisance from the footbridge construction works near Po Shun Road during nighttime.	Y	<p>According to the information provided and confirmed by the Engineer, night time construction works were only being conducted within site boundary under this contract on 27 March 2018. Therefore, no night time construction works were carried out on 10 March 2018.</p> <p>One valid Construction Noise Permit (CNP) (No. GW-RE0162-18) was granted to the Contractor for the construction works at Po Shun Road near Po Yap Road, one group of powered mechanical equipment (PME) will be allowed for any day not being holiday and not immediately following a general holiday from 00:30 - 05:30. Therefore, No violation of CNP was observed.</p> <p>The Contractor had implemented environmental measures to minimize noise nuisance to the nearby sensitive receivers as follows:</p> <ul style="list-style-type: none"> • The portable generator was enclosed by an acoustic enclosure. 	Closed

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
							<ul style="list-style-type: none"> The vibratory roller was operated with an acoustic baffle. <p>The following recommendations are made to further enhance the mitigation measures:</p> <ul style="list-style-type: none"> To regularly check and review the noise control activities that are being carried out on site to ensure compliance with statutory requirement. To locate noisy equipment as far away as possible from the NSR nearby. Machines and plant that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum. To provide training for the workers to prevent unnecessary noise disturbance. <p>The environmental conditions of the site and the control of works will be continuously reviewed and monitored by the Engineer and the Environmental Team.</p>	
137 ⁽⁵⁾	26 th March 2018	26 th March 2018 / Construction of Road P2	Anonymous	Air Quality	The complainant complained about dust/dirt being brought onto Tong Yin Street/Chin Shin Street by the vehicles travelling to and from TKO-LTT construction site, causing air nuisance and affecting the passerby/residents	N	<p>According to the information provided and confirmed by the Engineer, no dump truck was found improperly covered before leaving the site on 26 March 2018.</p> <p>According to the weekly site inspection conducted by the Environmental Team in March 2018, no observation was identified regarding dusty trail around site entrance nor dump truck leaving the site improperly covered/without wheel-washed. Manual wheel-washing was observed at the exit of the unloading area in Portion VII and the wheel-washing facility at the site exit was observed functioning properly.</p>	Closed
	27 th March 2018	26 th March 2018 / Construction of Road P2	Anonymous	Air Quality	The complainant complained that some of the excavated materials fell from the dump trucks and accumulated on the road near Tong Yin Street		<p>The Contractor had undertaken initiatives to minimize dust generation due to vehicle movement of dump trucks to the nearby sensitive receivers as follows:</p>	

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
					and Chi Shin Street.		<ul style="list-style-type: none"> • Immediately cleaned the dust and dirt on Tong Yin Street and Chi Shin Street; • Additional notice would be set up to remind the truck driver to perform wheel-washing properly before leaving site. <p>The Contractor has deployed staff at the access to check the dump trucks to ensure they are properly covered and wheel-washed before leaving the site</p> <p>The environmental conditions of the site and the control of works will be continuously reviewed and monitored by the Engineer and the Environmental Team.</p>	
138	27 th March 2018	Not specified / near Po Shun Road	Anonymous	Noise	The complainant complained the noise nuisance from the footbridge construction works near Po Shun Road from 12am to 5am.	Y	See Investigation / Mitigation Action for Complaint No. 136.	Closed
139	28 th March 2018	Not specified / near Po Shun Road	Resident of Park Central	Noise	The complainant complained the noise nuisance from the footbridge construction works near Po Shun Road during nighttime. She request to erect the noise barrier to minimize the noise nuisance to the nearby sensitive receiver.	Y		
140	28 th March 2018	Not specified / near Po Shun Road	Property Management Office of Park Central	Noise	The complainant complained the noise nuisance from the footbridge construction works near Po Shun Road during nighttime. He received few of complaints from resident and request to erect the	Y		

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
					noise barrier to minimize the noise nuisance to the nearby sensitive receiver.			
141	29 th March 2018	Not specified/ Not specified	Sai Kung District Council Member Mr. Chan Kai Wai	Noise	The complainant complained the noise nuisance from the marine work site due to the movement of barge.	Y	<p>According to the information provided and confirmed by the Engineer, one unit of derrick barge was mobilizing during the time of complaint on 29 March 2018. The frictional noise from the cable when moving the derrick barge is likely the source of noise nuisance.</p> <p>According to the information provided and confirmed by the Engineer, no land-based and marine-based construction works except general site cleanliness was performed on 8 April 2018. No noise impact would be expected from site cleanliness.</p> <p>One valid Construction Noise Permit (CNP) (No.: GW-RE0038-18) was granted to the Contractor for marine-based construction site near Ocean Shores, no use of powered mechanical equipment (PME) will be allowed for general holidays (including Sunday) at marine works area under this Contract. Since no land-based and marine-based construction activity was carried out on 8 April 2018 (Sunday), no violation of CNP is found in this regard.</p> <p>According to the Construction Noise Permit (CNP) (No.: GW-RE0038-18), no use of PME will be permitted for general holidays (including Sundays) at marine works area under this Contract. In this regard, the Contractor has utilized CCTV to keep track of the activities in marine portions and ensure no works are being conducted during restricted hours.</p> <p>For necessary PME operating during public holidays (including Sunday) on land-based works area, the Contractor is reminded to comply with the conditions of relevant CNPs and adopt good site practices recommended in the “Implementation Schedule of Proposed Mitigation Measures” of EM&A Manual and the approved Noise Mitigation Plan of this Contract, including the following:</p> <ul style="list-style-type: none"> • Only well-maintained plant should be operated on-site and plant should be serviced regularly during the 	Closed

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
							<p>construction program;</p> <ul style="list-style-type: none"> • Machines and plants that may be in intermittent use should be shut down between works periods or should be throttled down to minimum; • Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby noise sensitive receivers; <p>Furthermore, the Contractor had implemented environmental mitigation measures to minimize noise nuisance from construction barges as follows:</p> <ul style="list-style-type: none"> • Maintenance of barge including lubrication of moving parts was performed to minimize noise from worn or loose parts; • Noise source on barge was covered with acoustic materials • Nylon rope was used instead of wire rope to reduce the frictional noise when securing the barge in place <p>According to the regular noise monitoring conducted at Noise Monitoring Station CM6(A) and CM7(A), it is considered that no adverse noise impact was brought to the nearby sensitive receivers with the implementation of noise mitigation measures by the Contractor.</p> <p>The environmental conditions of the site and the control of works will be continuously reviewed and monitored by the Engineer and the Environmental Team.</p>	

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
142	29 th March 2018	Not specified / near Po Shun Road	Anonymous	Noise	The complainant complained the noise nuisance from the footbridge construction works near Po Shun Road during nighttime. He request to stop all construction work during nighttime.	Y	See Investigation / Mitigation Action for Complaint No. 136.	Closed
143	29 th March 2018	Not specified / near Tiu Keng Leng Road	Anonymous	Noise	The complainant complained the noise nuisance from the footbridge construction works near Tiu Keng Leng Road during nighttime on 27 th March 2018.	Y		
144	29 th March 2018	Not specified / near Po Shun Road	Public	Noise	The complainant complained about the noise arising from the footbridge construction works near Po Shun Road after midnight of 10 March 2018.	Y		
145	2 nd April 2018	Public holiday/ Construction Works near Eastern Harbour Crossing tunnel portal	Resident of Yau Lai Estate	Noise	The complainant complained the noise nuisance due to the construction work near Eastern Harbour Crossing tunnel portal on public holiday. (started from 9:00 am)	Y	Under Investigation	On-going
146	9 th April 2018	8 th April 2018/work site at the waterfront	Public	Noise	The complainant complaining about construction noise emanated from the work	Y	See Investigation / Mitigation Action for Complaint No. 142.	Closed

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
		near Ocean Shore			site at the waterfront near Ocean Shore Block 1 on 8 April 2018, starting from 8am. The complainant said noise were generated from barges, machine and construction vehicles and causing nuisance.			
147	15 th April 2018	Not specified/ Construction of Lam Tin Interchange	Resident of Yau Lai Estate	Noise	The complainant complained the noisy construction work at Lam Tin Interchange on public holiday.	Y	Under Investigation	On-going
148	15 th April 2018	Not specified/ Construction of Lam Tin Interchange	Resident of Yau Lai Estate	Noise	The complainant complained the noisy construction work at Lam Tin Interchange.	Y	Under Investigation	On-going
149	17 th April 2018	Not specified/ Construction of Lam Tin Interchange	Sham Shui Po District Council Member Mr. Ho Kai Ming	Noise	The complainant complained the noise nuisance during night time blasting works at the Lam Tin Interchange.	Y	Under Investigation	On-going
150	17 th April 2018	Not specified/ Construction of Lam Tin Interchange	Property Management Office of Yau Lai Estate	Noise	The complainant complained the noise nuisance due to the construction work at Lam Tin Interchange.	Y	Under Investigation	On-going
151	20 th April 2018	Not specified/ Construction of Lam Tin Interchange	Resident of Nga Lai Estate, Yau Lai Estate	Noise	The complainant complained the noise nuisance during night time blasting works at the Lam Tin Interchange.	Y	Under Investigation	On-going
152	23 th April 2018	Not specified/ Construction of Lam Tin Interchange	Resident of Yau Lai Estate	Noise	The complainant complained the noisy breaking work from two breakers at Lam Tin Interchange. He requested the Contractor to review the noise mitigation measures on site.	Y	Under Investigation	On-going

Complaint No.	Received Date	Date/Location of Complaint	Complainant	Nature	Details of Complaint	Noise Action Level Exceedance (Y/N)	Investigation/ Mitigation Action	File Closed
153	23 th April 2018	Not specified/ Construction of Lam Tin Interchange	Kwun Tong District Council Member Mr. Lai Shu Ho	Noise	The complainant complained the noise nuisance during night time blasting works at the Lam Tin Interchange.	Y	Under Investigation	On-going
154	23 th April 2018	Not specified / Construction of Road P2	Public	Noise	The complainant complained about noise from construction activities at the sea area near Ocean Shore Block 6 starting 8:30-8:45am on 23 April 2018. She suspected the noise is from drilling/breaking works.	Y	Under Investigation	On-going
155	25 th April 2018	Not specified/ Construction of Lam Tin Interchange	Resident of Yau Lai Estate, Yau Lai Estate	Noise	The complainant complained the noise nuisance due to the breaking work at Lam Tin Interchange.	Y	Under Investigation	On-going
156	26 th April 2018	Not specified / Construction of TKO portal	Resident of Laguna City	Light	The complainant complained that two spotlights were used during daytime and nighttime causing light nuisance to the residents. She requested to direct the strong lighting toward the sea.	N	Under Investigation	On-going
157	30 th April 2018	Not specified/ Construction of Lam Tin Interchange	Property Management Office of Kwong Tin Estate	Noise	The complainant complained the noise nuisance due to the breaking work at Lam Tin Interchange.	Y	Under Investigation	On-going
158	30 th April 2018	Not specified / Construction of Road P2	Public	Noise & Odour	The complainant complained the construction noise and odour nuisance from the construction vessel.	Y	Under Investigation	On-going

Note:

(1) Previous case received on 01 March 2018 on air quality near Cha Kwo Ling Tsuen and Tin Hau Temple is confirmed to be non-project related.

- (2) Previous case received on 20 March 2018 on landscape and visual impact near Cha Kwo Ling Road is confirmed to be non-project related.
- (3) Previous case received on 27 March 2018 on construction noise nuisance in TKO portal is confirmed to be Enquiry on the Project instead of a documented complaint.
- (4) Two environmental complaints received on 3 March 2018 have been updated in the above table.
- (5) For the Case 137, it is noted that the same complaint was received on 26 & 27 March 2018 through different channels regarding the same issue on 26 March 2018. Therefore, it is considered as ONE number of complaint.

Cumulative Complaint Log since commencement of Project

Reporting Month	Number of Complaints in Reporting Month	Number of Summons in Reporting Month	Number of Prosecutions in Reporting Month
November 2016	0	0	0
December 2016	11	0	0
January 2017	15	0	0
February 2017	4	0	0
March 2017	6	0	0
April 2017	1	0	0
May 2017	10	0	0
June 2017	8	0	0
July 2017	3	0	0
August 2017	8	0	0
September 2017	14	0	0
October 2017	8	0	0
November 2017	12	0	0
December 2017	10	1	0
January 2018	11	0	0
February 2018	6	0	0
March 2018	17*	0	0
April 2018	14	0	0
Total	161	1	0

Note (*): The Number of Complaints in March 2018 has been updated.

Cumulative Log for Notifications of Summons

Contract No.	Log Ref.	Date/Location	Subject	Status	Total no. Received in this reporting month	Total no. Received since project commencement
NE/2015/01	--	--	--	--	--	--
NE/2015/02	KTS2 4138/ 2017	25 June 2017/ Marine construction site at Junk Bay	Contrary to: Sections 6 (1) (b) and 6 (5), Noise Control Ordinance, Cap.400	First hearing on 29 Mar 2018	0	1
NE/2015/03	--	--	--	--	--	--
NE/2017/01	--	--	--	--	--	--
NE/2017/02	--	--	--	--	--	--

Cumulative Log for Successful Prosecutions

Contract No.	Log Ref.	Date/Location	Subject	Status	Total no. Received in this reporting month	Total no. Received since project commencement
NE/2015/01	--	--	--	--	--	--
NE/2015/02	--	--	--	--	--	--
NE/2015/03	--	--	--	--	--	--
NE/2017/01	--	--	--	--	--	--
NE/2017/02	--	--	--	--	--	--

**APPENDIX P
WASTE GENERATION IN THE
REPORTING MONTH**



Monthly Summary Waste Flow Table for 2018

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	a.Total Quantity Generated (see Note 8)	b. Hard Rock and Large Broken Concrete	c. Reused in the Contract	d. Reused in Other Projects	e. Disposed as Public Fill (see Note 10)	f. Imported Fill	g. Metals (see Note 5)	h. Paper / Cardboard Packaging (see Note 5)	i. Plastics (see Note 3) (see Note 5)	j. Chemical Waste	k. Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
January	118.887	44.216	25.727	60.437	32.723	0.000	0.000	0.308	0.000	1.200	0.094
February	76.419	34.880	8.626	54.212	13.581	0.000	0.000	0.000	0.000	0.800	0.046
March	140.974	31.352	57.578	49.166	34.230	0.000	0.000	0.020	0.000	0.000	0.052
April	123.925	30.310	57.340	42.266	24.319	0.000	0.000	0.368	0.000	1.200	0.058
May											
June											
Sub-total	460.205	140.758	149.271	206.081	104.853	0.000	0.000	0.696	0.000	3.200	0.250
July											
August											
September											
October											
November											
December											
Total	460.205	140.758	149.271	206.081	104.853	0.000	0.000	0.696	0.000	3.200	0.250

Total inert C&D waste generated = c+d+e

Total inert C&D waste recycled = c+d

% of recycled inert C&D waste = Total C&D waste recycled / Total C&D waste generated



- Notes: (1) The performance target are given in PS Clause 6(14)
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material
- (4) The Contractor shall also submit the latest forecast of the amount of C&D materials expected to be generated from the Works, together with a break down of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000m³. (PS Clause 1.105(4) refers)
- (5) All recyclable materials, including metals, paper / cardboard packaging, plastics, etc. will be collected by registered collector for recycling.
- (6) Conversion factors for reporting purpose:
in-situ: rock = 2.5 tonnes/m³; soil = 2.0 tonnes/m³
- (7) excavated: rock = 2.0 tonnes/m³; soil = 1.8 tonnes/m³; broken concrete and bitumen = 2.4 tonnes/m³, soil and rock = 1.9 tonnes/m³
- (8) C&D Waste = 0.9 tonnes/m³; bentonite slurry = 2.8 tonnes/m³
Diesel density: 0.8kg/l
Numbers are rounded off to the nearest three decimal places
The "Total Quantity Generated" equals to the sum of "Reuse in the Contract", "Reuse in Other Projects" and "Disposed as Public Fill"

Monthly Summary Waste Flow Table for 2018 Year

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Borken Concrete	Reused in the Contract	Reused in other Projects	Disposal as Public Fill	Imported Fill	Metals	Paper / Cardboard Packaging	Plastics (See note 3)	Chemical Waste	Other, e.g. general refuse
	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000kg]	[in '000kg]	[in '000kg]	[in '000kg]	[in '000m ³]
Jan	0.30510	0.00000	0.11060	0.00000	0.00850	0.18600	0.00000	0.00000	0.00000	0.00000	0.07544
Feb	1.12247	0.00000	0.01080	0.00000	1.08367	0.02800	32.04000	0.00000	0.00000	0.00000	0.05240
Mar	6.50826	0.00000	0.04500	0.00000	6.46326	0.00000	10.46000	0.00000	0.00000	0.00000	0.04520
Apr	77.68090	0.00000	0.00000	0.00000	3.82690	73.85400	14.78000	0.00000	0.00000	0.00000	0.03010
May											
June											
SUB-TOTAL	85.61673	0.00000	0.16640	0.00000	11.38233	74.06800	57.28000	0.00000	0.00000	0.00000	0.20314
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
TOTAL	85.61673	0.00000	0.16640	0.00000	11.38233	74.06800	57.28000	0.00000	0.00000	0.00000	0.20314

Note: Conversion to 1000m³ for general refuse is weight in 1000kg multiply by 0.002

Conversion to 1000m³ for Inert C&D is weight in 1000kg multiply by 0.0005

Plastics refer to plastic bottles / containers, plastic sheets / foam from packaging material

Plastics refer to plastic bottles / containers, plastic sheets / foam from packaging material



Monthly Summary of Waste Flow Table for 2018

Name of Person completing the Record: Ricky Hon

Month	Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
		<i>(see Note 1)</i>						<i>(see Note 2)</i>		
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 Kg)	(in '000 Kg)	(in '000 Kg)	(in '000 Kg)	(in '000m ³)
Jan	0	0	0	0	0	0	0	0	0	0
Feb	0	0	0	0	0	0	0	0	0	0.143
Mar	0	0	0	0	0	0	0	0	0	0
Apr	0	0	0	0	0	0	0	0	0	0.0975
May										
Jun										
Sub-total	0	0	0	0	0	0	0	0	0	0.2405
Jul										
Aug										
Sept										
Oct										
Nov										
Dec										
Total	0	0	0	0	0	0	0	0	0	0.2405

Notes:

- (1) Broken concrete for recycling into aggregates.
- (2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- (3) Use the conversion factor: 1 full load of dumping truck being equivalent to 6.5m³ by volume.

Name of Department : CEDD

Contract No. : NE/2015/03

Monthly Summary Waste Flow Table for 2018 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock & Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemicals Waste	Others, e.g. general refuse
	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 m ³)
Accumulated From 2017	0.84697	0	0.175365	0.290915	0.350135	0.03056	0	0	0	0	0.03079
Jan	0.2397525	0	0	0.0642025	0.17555	0	0	0	0	0	0.00614
Feb	0.0722875	0	0	0.0722875	0	0	0	0	0	0	0
Mar	0.05853	0	0	0	0.05853	0	0	0	0	0	0
Apr	0.007575	0	0	0	0.007575	0	0	0	0	0	0
May											
June											
Sub-total											
July											
Aug											
Sept											
Oct											
Nov											
Dec											
Total	1.225109	0	0.175365	0.427405	0.59179	0.03056	0	0	0	0	0.03693

- Notes:
- (1) The performance targets are given in PS Clause 6.14.
 - (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
 - (4) The *Contractor* shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the *works*, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the *works* is equal to or exceeding 50,000 ms.

Monthly Summary Waste Flow Table for 2018

Name of Department: Civil Engineering and Development Department

Contract No.: NE/2017/01

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan	0	0	0	0	0	0	0	0	0	0	0
Feb	0	0	0	0	0	0	0	0	0	0	0
Mar	0	0	0	0	0	0	0	0	0	0	0
Apr	0	0	0	0	0	0	0	0	0	0	0
May											
Jun											
Sub-total	0	0	0	0	0	0	0	0	0	0	0
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
Total	0	0	0	0	0	0	0	0	0	0	0

- Notes:
1. Assume the density of soil fill is 2 ton/m³.
 2. Assume the density of rock and broken concrete is 2.5 ton/m³.
 3. Assume each truck of C&D wastes is 5m³.
 4. The inert C&D materials except slurry and bentonite are disposed at Tseung Kwan O Area 137 Fill Bank.
 5. The slurry and bentonite are disposed at Tseung Kwan O Area 137 Fill Bank.
 6. The non-inert C&D wastes are disposed at NENT.
 7. Assume the density of metal is 7,850 kg/m³.
 8. Assume the density of plastic is 941 kg/m³.

**APPENDIX Q
TENTATIVE CONSTRUCTION
PROGRAMME**

High Level 3 Months Look Ahead Programme

Activities	Apr-18	May-18	Jun-18
Lam Tin Interchange			
EHC2 U-Trough			
Site Formation - Area 1G1 & 1G2 &5			
Site Formation - Area 2			
Site Formation - Area 3			
Site Formation - Area 4			
Soldier Pile Wall - Area 2A			
Main Tunnel			
MT Excavation			
TKO Interchange			
Haul Road Construction, Site Formation & Slope Works			
Steel Platform for Bridge Construction			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance - BL1	2018					
											Apr	May	Jun	Jul	Aug	
NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)																
Preliminaries, Submission, Contractor's Design Submission and Approval																
Preliminaries																
Design Submission of Physical Model																
LC10242	Design the Physical Model	P2-Cal.A	14	14	20-Apr-18	03-May-18	642	0%		0						
LC10244	Review and Discuss the Physical Model	P2-Cal.A	21	21	04-May-18	24-May-18	642	0%		0						
LC10246	Resubmission of Physical Model	P2-Cal.A	14	14	25-May-18	07-Jun-18	642	0%		0						
LC10248	Approve the Physical Model	P2-Cal.A	21	21	08-Jun-18	28-Jun-18	642	0%		0						
LC10250	Fabrication of Physical Model	P2-Cal.A	90	90	29-Jun-18	26-Sep-18	642	0%		0						
General Submission and Acceptance																
S10050	Submission of the Temporary Drainage Management Plan incorporating the mitigation plan for diversion of DN1500	P2-Cal.A	60	10	20-Nov-17 A	29-Apr-18	-168	83.33%		-101						
S10240	Prepare/Submit the Weather Protection Scheme	P2-Cal.A	30	20	21-Aug-17 A	09-May-18	782	33.33%		-232						
Contractor's Design Submission and Acceptance																
Foundation Design																
AIP Submission for Foundation of Road P2 Structure (Reclaimed Section) Zone 1 CT01 CH366.059-201.44																
S11260-1	2nd Resubmit AIP Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 1)	P2-Cal.A	14	2	30-May-17 A	21-Apr-18	-76	85.71%		-313						
S11260-2	Review and Accept AIP Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 1)	P2-Cal.A	21	21	22-Apr-18	12-May-18	-76	0%		0						
AIP Submission for Foundation of Road P2 Structure (Reclaimed Section) Zone 2 (S200 CH821 - P2 CH188)																
S11269-1	2nd Resubmit AIP Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 2)	P2-Cal.A	14	2	27-Jul-17 A	21-Apr-18	-76	85.71%		-255						
S11270	Review and Accept AIP Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 2)	P2-Cal.A	21	21	22-Apr-18	12-May-18	-76	0%		0						
AIP Submission for Foundation of Road P2 Structure (Reclaimed Section) Zone 3 (P2 CH188 - CH278)																
S11278-2	2nd Resubmit AIP Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 3)	P2-Cal.A	14	2	27-Jul-17 A	21-Apr-18	-76	85.71%		-255						
S11279	Review and Accept AIP Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 3)	P2-Cal.A	21	21	22-Apr-18	12-May-18	-76	0%		0						
DDA Submission for Foundation of Road P2 Structure (Reclaimed Section) Zone 1 CT01 CH366.059-201.44																
S11360	Prepare and Submit DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 1)	P2-Cal.A	21	21	13-May-18	02-Jun-18	-76	0%		0						
S11380	Review and Discuss DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 1)	P2-Cal.A	21	21	03-Jun-18	23-Jun-18	-76	0%		0						
S11400	Resubmit DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 1)	P2-Cal.A	14	14	24-Jun-18	07-Jul-18	-76	0%		0						
S11410	Review and comment by GEO	P2-Cal.A	14	14	08-Jul-18	21-Jul-18	-76	0%		0						
DDA Submission for Foundation of Road P2 Structure (Reclaimed Section) Zone 2 (S200 CH821 - P2 CH188)																
S11422	Prepare and Submit DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 2)	P2-Cal.A	21	21	13-May-18	02-Jun-18	-76	0%		0						
S11424	Review and Discuss DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 2)	P2-Cal.A	21	21	03-Jun-18	23-Jun-18	-76	0%		0						
S11426	Resubmit DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 2)	P2-Cal.A	14	14	24-Jun-18	07-Jul-18	-76	0%		0						
S11428	Review and comment by GEO	P2-Cal.A	14	14	08-Jul-18	21-Jul-18	-76	0%		0						
DDA Submission for Foundation of Road P2 Structure (Reclaimed Section) Zone 3 (P2 CH188 - CH278)																
S11432	Prepare and Submit DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 3)	P2-Cal.A	21	21	13-May-18	02-Jun-18	-76	0%		0						
S11434	Review and Discuss DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 3)	P2-Cal.A	21	21	03-Jun-18	23-Jun-18	-76	0%		0						
S11436	Resubmit DDA Submission for Foundation of Road P2 Structure (Reclaimed Section Zone 3)	P2-Cal.A	14	14	24-Jun-18	07-Jul-18	-76	0%		0						
S11438	Review and comment by GEO	P2-Cal.A	14	14	08-Jul-18	21-Jul-18	-76	0%		0						
E&M Design																
Statutory Approval for E&M Works																
S11570-11	FSD Approval for Underpass GBP	P2-Cal.A	0	0	15-Jun-18	15-Jun-18	32	0%		0						
S11570-12	FSD Approval for Plant room GBP	P2-Cal.A	0	0	15-Jun-18	15-Jun-18	32	0%		0						
Detail Design for E&M Works (Tunnel and associated)																

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)

Page :1 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance - BL1	2018				
											Apr	May	Jun	Jul	Aug
MVAC Detail Design											MVAC Detail Design				
Plantroom											Plantroom				
S11575	Design Coordination for MVAC services	P2-Cal.A	60	8	25-Apr-17 A	27-Apr-18	49	86.67%		-308	Design Coordination for MVAC services				
S11576-02	3rd Review by EMSD/HyD	P2-Cal.A	15	3	09-Mar-18 A	30-Apr-18	49	80%		-38	3rd Review by EMSD/HyD				
S11577	Formal Submission to Supervisor	P2-Cal.A	8	8	01-May-18	08-May-18	49	0%		0	Formal Submission to Supervisor				
S11578	Accept detail design by the Supervisor	P2-Cal.A	7	7	09-May-18	15-May-18	49	0%		0	Accept detail design by the Supervisor				
Underpass											Underpass				
S11627	3rd review by EMSD/HyD	P2-Cal.A	15	11	16-Mar-18 A	30-Apr-18	49	26.67%		-31	3rd review by EMSD/HyD				
S11630	Formal Submission to Supervisor	P2-Cal.A	8	8	01-May-18	08-May-18	49	0%		0	Formal Submission to Supervisor				
S11640	Accept detail design by the Supervisor	P2-Cal.A	7	7	09-May-18	15-May-18	49	0%		0	Accept detail design by the Supervisor				
FS Detail Design											FS Detail Design				
Underpass											Underpass				
S11649	FSD review GBP	P2-Cal.A	28	7	19-Oct-17 A	26-Apr-18	32	75%		-162	FSD review GBP				
S11650-01	2nd review by EMSD	P2-Cal.A	15	13	19-Mar-18 A	09-May-18	32	13.33%		-37	2nd review by EMSD				
S11651	Accept detail design by the Supervisor	P2-Cal.A	7	7	10-May-18	16-May-18	32	0%		0	Accept detail design by the Supervisor				
Plantroom											Plantroom				
S11652-10	FSD review GBP	P2-Cal.A	28	7	19-Oct-17 A	26-Apr-18	32	75%		-162	FSD review GBP				
S11652-21	2nd review by FSD/EMSD	P2-Cal.A	15	13	19-Mar-18 A	09-May-18	32	13.33%		-37	2nd review by FSD/EMSD				
S11652-23	Accept detail design by the Supervisor	P2-Cal.A	7	7	10-May-18	16-May-18	32	0%		0	Accept detail design by the Supervisor				
Plumbing and Drainage Detail Design											Plumbing and Drainage Detail Design				
Underpass											Underpass				
S11656	Design Coordination for PD Services	P2-Cal.A	60	7	03-May-17 A	26-Apr-18	47	88.33%		-299	Design Coordination for PD Services				
S11657	1st review by HyD/EMSD	P2-Cal.A	15	7	09-Apr-18 A	03-May-18	47	53.33%		-10	1st review by HyD/EMSD				
S11658	Formal Submission to Supervisor	P2-Cal.A	7	7	04-May-18	10-May-18	47	0%		0	Formal Submission to Supervisor				
S11659	Accept detail design by the Supervisor	P2-Cal.A	7	7	11-May-18	17-May-18	47	0%		0	Accept detail design by the Supervisor				
Plantroom											Plantroom				
S11660-08	Design Coordination for PD Services	P2-Cal.A	60	7	01-Apr-17 A	26-Apr-18	47	88.33%		-331	Design Coordination for PD Services				
S11660-09	1st review by HyD/EMSD	P2-Cal.A	15	7	09-Mar-18 A	03-May-18	47	53.33%		-41	1st review by HyD/EMSD				
S11660-10	Formal Submission to Supervisor	P2-Cal.A	7	7	04-May-18	10-May-18	47	0%		0	Formal Submission to Supervisor				
S11660-11	Accept detail design by the Supervisor	P2-Cal.A	7	7	11-May-18	17-May-18	47	0%		0	Accept detail design by the Supervisor				
Electrical Detail Design											Electrical Detail Design				
Underpass Lighting											Underpass Lighting				
S11660-16	1st review by EMSD/HyD	P2-Cal.A	15	15	26-Jul-17 A	04-May-18	46	0%		-268	1st review by EMSD/HyD				
S11660-18	Formal Submission to Supervisor	P2-Cal.A	7	7	05-May-18	11-May-18	46	0%		0	Formal Submission to Supervisor				
S11660-19	Accept detail design by the Supervisor	P2-Cal.A	7	7	12-May-18	18-May-18	46	0%		0	Accept detail design by the Supervisor				
External Road Lighting											External Road Lighting				
S11660-24	1st review by EMSD/CLP/ HyD	P2-Cal.A	15	15	08-Sep-17 A	04-May-18	60	0%		-224	1st review by EMSD/CLP/ HyD				
S11660-26	Formal Submission to Supervisor	P2-Cal.A	7	7	05-May-18	11-May-18	60	0%		0	Formal Submission to Supervisor				
S11660-27	Accept detail design by the Supervisor	P2-Cal.A	7	7	12-May-18	18-May-18	60	0%		0	Accept detail design by the Supervisor				
Plantroom											Plantroom				
S11665	Design Coordination for EL Services	P2-Cal.A	60	10	07-Mar-17 A	29-Apr-18	36	83.33%		-359	Design Coordination for EL Services				
S11666	1st review by EMSD/HyD	P2-Cal.A	15	15	20-Apr-18 A	14-May-18	36	0%		-10	1st review by EMSD/HyD				
S11667	Formal Submission to Supervisor	P2-Cal.A	7	7	15-May-18	21-May-18	36	0%		0	Formal Submission to Supervisor				

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)

Page :2 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance - BL1	2018						
											Apr	May	Jun	Jul	Aug		
S11668	Accept detail design by the Supervisor	P2-Cal.A	7	7	22-May-18	28-May-18	36	0%		0							
ELV And SCADA Detail Design		P2-Cal.A	157	36	12-Aug-17 A	25-May-18	39			-130							
Underpass		P2-Cal.A	157	36	12-Aug-17 A	25-May-18	39			-130							
S11669-10	Design Coordination for ELV & SCADA	P2-Cal.A	60	10	12-Aug-17 A	29-Apr-18	39	83.33%		-201							
S11669-19	2nd review by HyD	P2-Cal.A	15	12	17-Apr-18 A	11-May-18	39	20%		-10							
S11669-29	Formal Submission to Supervisor	P2-Cal.A	7	7	12-May-18	18-May-18	39	0%		0							
S11669-30	Accept detail design by the Supervisor	P2-Cal.A	7	7	19-May-18	25-May-18	39	0%		0							
Plantroom		P2-Cal.A	118	36	12-Aug-17 A	25-May-18	39			-169							
S11670-10	Design Coordination for ELV & SCADA	P2-Cal.A	10	10	12-Aug-17 A	29-Apr-18	39	0%		-251							
S11670-19	2nd review by HyD	P2-Cal.A	15	12	17-Apr-18 A	11-May-18	39	20%		-10							
S11670-29	Formal Submission to Supervisor	P2-Cal.A	7	7	12-May-18	18-May-18	39	0%		0							
S11670-30	Accept detail design by the Supervisor	P2-Cal.A	7	7	19-May-18	25-May-18	39	0%		0							
Design of Architectural Finishes for Internal Walls of U-Trough Structures		P2-Cal.A	77	77	25-Apr-18	10-Jul-18	18			0							
S11675	Prepare and Submit Design of Architectural Finishes for Internal Walls of U-Trough Structures (VE and PC Panel)	P2-Cal.A	21	21	25-Apr-18	15-May-18	18	0%		0							
S11680	Review and Discuss Design of Architectural Finishes for Internal Walls of U-Trough Structures (VE and PC Panel)	P2-Cal.A	21	21	16-May-18	05-Jun-18	18	0%		0							
S11700	Resubmit Design of Architectural Finishes for Internal Walls of U-Trough Structures (VE and PC Panel)	P2-Cal.A	14	14	06-Jun-18	19-Jun-18	18	0%		0							
S11720	Review and Accept Design of Architectural Finishes for Internal Walls of U-Trough Structures (VE and PC Panel)	P2-Cal.A	21	21	20-Jun-18	10-Jul-18	18	0%		0							
Irrigation System		P2-Cal.A	139	108	01-Feb-18 A	05-Aug-18	41			-47							
S11786	Reviewed by Supervisor	P2-Cal.A	21	10	01-Feb-18 A	29-Apr-18	41	52.38%		-67							
S11787	1st review by LCSD/EMSD	P2-Cal.A	21	21	30-Apr-18	20-May-18	41	0%		0							
S11788	Prepare & Submission of Form 542	P2-Cal.A	14	14	21-May-18	03-Jun-18	41	0%		0							
S11789	Reviewed by WSD	P2-Cal.A	28	28	04-Jun-18	01-Jul-18	41	0%		0							
S11790	Formal Submission to Supervisor	P2-Cal.A	14	14	02-Jul-18	15-Jul-18	41	0%		0							
S11800	Review and Accept Submission for Waterpoints and associated elements	P2-Cal.A	21	21	16-Jul-18	05-Aug-18	41	0%		0							
Contractor Cost Saving Design		P2-Cal.A	161	102	02-Feb-18 A	30-Jul-18	108			-18							
AIP Submission for CSD2 of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355)		P2-Cal.A	140	81	02-Feb-18 A	09-Jul-18	-92			-18							
S11925	Resubmit AIP for CSD of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355)	P2-Cal.A	21	4	02-Feb-18 A	23-Apr-18	-92	80.95%		-60							
S11930	Review and Discuss AIP Submission for CSD of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355)	P2-Cal.A	21	21	24-Apr-18	14-May-18	-92	0%		0							
S11940	Resubmit AIP for CSD of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355)	P2-Cal.A	28	28	15-May-18	11-Jun-18	-92	0%		0							
S11950	Review and Accept AIP Submission for CSD of Reclaimed Section by CEDD (S200 CH674 - CH755, S300 CH326-CH355)	P2-Cal.A	21	21	12-Jun-18	02-Jul-18	-85	0%		0							
S11960	Review and Accept AIP Submission for CSD of Reclaimed Section by HYD (S200 CH674 - CH755, S300 CH326-CH355)	P2-Cal.A	28	28	12-Jun-18	09-Jul-18	-92	0%		0							
DDA Submission for CSD2 of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355)		P2-Cal.A	21	21	10-Jul-18	30-Jul-18	-92			0							
S11962	Prepare and Submit DDA Submission for CSD of Reclaimed Section (S200 CH674 - CH755, S300 CH326-CH355)	P2-Cal.A	21	21	10-Jul-18	30-Jul-18	-92	0%		0							
AIP Submission for CSD3 of Reclaimed Section (S200 CH821 - P2 CH305)		P2-Cal.A	140	81	02-Feb-18 A	09-Jul-18	108			-18							
S11970	Prepare and Submit AIP Submission for CSD of Reclaimed Section (S200 CH821 - P2 CH305)	P2-Cal.A	21	4	02-Feb-18 A	23-Apr-18	108	80.95%		-60							
S11971	Review and Discuss AIP Submission for CSD of Reclaimed Section (S200 CH821 - P2 CH305)	P2-Cal.A	21	21	24-Apr-18	14-May-18	108	0%		0							
S11972	Resubmit AIP Submission for CSD of Reclaimed Section (S200 CH821 - P2 CH305)	P2-Cal.A	28	28	15-May-18	11-Jun-18	108	0%		0							
S11973	Review and Accept AIP Submission for CSD of Reclaimed Section by CEDD (S200 CH821 - P2 CH305)	P2-Cal.A	21	21	12-Jun-18	02-Jul-18	115	0%		0							
S11974	Review and Accept AIP Submission for CSD of Reclaimed Section by HyD (S200 CH821 - P2 CH305)	P2-Cal.A	28	28	12-Jun-18	09-Jul-18	108	0%		0							
DDA Submission for CSD3 of Reclaimed Section (S200 CH821 - P2 CH305)		P2-Cal.A	21	21	10-Jul-18	30-Jul-18	108			0							
S11975	Prepare and Submit DDA Submission for CSD of Reclaimed Section (S200 CH821 - P2 CH305)	P2-Cal.A	21	21	10-Jul-18	30-Jul-18	108	0%		0							
Major Temporary Works Design		P2-Cal.A	122	74	06-Feb-18 A	02-Jul-18	78			-25							
Temporary Jetty Design		P2-Cal.A	28	28	13-Apr-18 A	17-May-18	-151			-7							

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)
Page :3 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance - BL1	2018						
											Apr	May	Jun	Jul	Aug		
S13060	Resubmit Temporary Jetty Design	P2-Cal.A	14	7	13-Apr-18 A	26-Apr-18	-151	50%		0							
S13080	Accept Temporary Jetty Design	P2-Cal.A	21	21	27-Apr-18	17-May-18	-151	0%		0							
Design of Marine Survey Tower		P2-Cal.A	74	74	20-Apr-18	02-Jul-18	24			0							
S13100	Prepare and Submit Marine Survey Tower	P2-Cal.A	18	18	20-Apr-18	07-May-18	24	0%		0							
S13120	Review and Discuss Marine Survey Tower	P2-Cal.A	21	21	08-May-18	28-May-18	24	0%		0							
S13140	Resubmit Temporary Marine Survey Tower	P2-Cal.A	14	14	29-May-18	11-Jun-18	24	0%		0							
S13160	Accept Temporary Marine Survey Tower	P2-Cal.A	21	21	12-Jun-18	02-Jul-18	24	0%		0							
ELS Design for Retaining Wall of P2-A (Bay 1 - 3)		P2-Cal.A	72	24	06-Feb-18 A	13-May-18	128			-25							
S13181	Prepare and Submit ELS Design for Retaining Wall of P2-A (Bay 1 - 3)	P2-Cal.A	28	3	06-Feb-18 A	22-Apr-18	128	89.29%		-48							
S13184	Accept ELS Design for Retaining Wall of P2-A (Bay 1 - 3)	P2-Cal.A	21	21	23-Apr-18	13-May-18	128	0%		0							
Major Construction Works Method Statement		P2-Cal.A	105	105	29-Mar-18 A	02-Aug-18	-30			-22							
Ground Treatment for Reclamation		P2-Cal.A	33	23	07-Apr-18 A	12-May-18	-201			-3							
S13304	Resubmit Method Statement for Ground Treatment for Reclamation	P2-Cal.A	7	2	07-Apr-18 A	21-Apr-18	-201	71.43%		-8							
S13320	Accept Method Statement for Ground Treatment for Reclamation	P2-Cal.A	21	21	22-Apr-18	12-May-18	-201	0%		0							
Reclamation Filling		P2-Cal.A	26	23	29-Mar-18 A	12-May-18	-202			-19							
S13384	Resubmit Method Statement for Reclamation Filling	P2-Cal.A	7	2	29-Mar-18 A	21-Apr-18	-202	71.43%		-17							
S13400	Accept Method Statement for Reclamation Filling	P2-Cal.A	21	21	22-Apr-18	12-May-18	-202	0%		0							
Removal of Temporary Steel Cofferdam		P2-Cal.A	67	67	20-May-18	25-Jul-18	-69			0							
S13810	Prepare and Submit Method Statement for Removal of Temporary Steel Cofferdam (type 1)	P2-Cal.A	18	18	20-May-18	06-Jun-18	-69	0%		0							
S13811	Review and Discuss Method Statement for Removal of Temporary Steel Cofferdam (type 1)	P2-Cal.A	21	21	07-Jun-18	27-Jun-18	-69	0%		0							
S13812	Resubmit Method Statement for Removal of Temporary Steel Cofferdam (type 1)	P2-Cal.A	7	7	28-Jun-18	04-Jul-18	-69	0%		0							
S13813	Accept Method Statement for Removal of Temporary Steel Cofferdam (type 1)	P2-Cal.A	21	21	05-Jul-18	25-Jul-18	-69	0%		0							
ELS of Underpass (P2 CH105-318)		P2-Cal.A	67	67	28-May-18	02-Aug-18	-30			0							
S14056	Prepare and Submit Method Statement for Excavation and ELS of Underpass (P2 CH105-318)	P2-Cal.A	18	18	28-May-18	14-Jun-18	-30	0%		0							
S14057	1st Review and Discuss Method Statement for Excavation and ELS of Underpass (P2 CH105-318)	P2-Cal.A	21	21	15-Jun-18	05-Jul-18	-30	0%		0							
S14058	Resubmit Method Statement for Excavation and ELS of Underpass (P2 CH105-318)	P2-Cal.A	7	7	06-Jul-18	12-Jul-18	-30	0%		0							
S14059	Accept Method Statement for Excavation and ELS of Underpass (P2 CH105-318)	P2-Cal.A	21	21	13-Jul-18	02-Aug-18	-30	0%		0							
ELS of U-Troughs (P2 CH318-363)		P2-Cal.A	67	67	28-May-18	02-Aug-18	-144			0							
S14060	Prepare and Submit Method Statement for Excavation and ELS of U-Troughs (P2 CH318-363)	P2-Cal.A	18	18	28-May-18	14-Jun-18	-144	0%		0							
S14080	1st Review and Discuss Method Statement for Excavation and ELS of U-Troughs (P2 CH318-363)	P2-Cal.A	21	21	15-Jun-18	05-Jul-18	-144	0%		0							
S14100	Resubmit Method Statement for Excavation and ELS of U-Troughs (P2 CH318-363)	P2-Cal.A	7	7	06-Jul-18	12-Jul-18	-144	0%		0							
S14120-01	Accept Method Statement for Excavation and ELS of U-Troughs (P2 CH318-363)	P2-Cal.A	21	21	13-Jul-18	02-Aug-18	-144	0%		0							
Construction of U-Troughs structure (P2 CH318-363)		P2-Cal.A	74	74	18-May-18	30-Jul-18	-42			0							
S14122	Prepare and Submit Method Statement for Construction of U-Troughs Structure (P2 CH318-363)	P2-Cal.A	18	18	18-May-18	04-Jun-18	-42	0%		0							
S14124	Review and Discuss Method Statement for Construction of U-Troughs Structure (P2 CH318-363)	P2-Cal.A	21	21	05-Jun-18	25-Jun-18	-42	0%		0							
S14126	Resubmit Method Statement for Construction of U-Troughs Structure (P2 CH318-363)	P2-Cal.A	14	14	26-Jun-18	09-Jul-18	-42	0%		0							
S14128	Accept Method Statement for Construction of U-Troughs Structure (P2 CH318-363)	P2-Cal.A	21	21	10-Jul-18	30-Jul-18	-42	0%		0							
Treatment of Dredged Marine Sediment of Type 1		P2-Cal.A	30	26	11-Apr-18 A	15-May-18	-205			-5							
S14375-02	Submit Method Statement for Treatment of Dredging Marine Sediment of Type 1	P2-Cal.A	14	5	11-Apr-18 A	24-Apr-18	-205	64.29%		0							
S14376	Accept Method Statement for Treatment of Dredging Marine Sediment of Type 1	P2-Cal.A	21	21	25-Apr-18	15-May-18	-205	0%		0							
Construction of Vertical Seawall		P2-Cal.A	35	37	29-Mar-18 A	26-May-18	-198			-24							
S14933	Review and Discuss Method Statement for Construction of Vertical Seawall	P2-Cal.A	21	2	29-Mar-18 A	21-Apr-18	-198	90.48%		-3							
S14935	Resubmit Method Statement for Construction of Vertical Seawall	P2-Cal.A	14	14	22-Apr-18	05-May-18	-198	0%		0							

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)

Page :4 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance-BL1	2018					
											Apr	May	Jun	Jul	Aug	
S14937	Accept Method Statement for Construction of Vertical Seawall	P2-Cal.A	21	21	06-May-18	26-May-18	-198	0%		0						
Construction of Vertical Band Drain																
S14939	Prepare and Submit Method Statement for Construction of Vertical Band Drain	P2-Cal.A	5	5	20-Apr-18	24-Apr-18	-180	0%		0						
S14941	Review and Discuss Method Statement for Construction of Vertical Band Drain	P2-Cal.A	21	21	25-Apr-18	15-May-18	-180	0%		0						
S14945	Resubmit Method Statement for Construction of Vertical Band Drain	P2-Cal.A	3	3	16-May-18	18-May-18	-180	0%		0						
S14947	Accept Method Statement for Construction of Vertical Band Drain	P2-Cal.A	14	14	19-May-18	01-Jun-18	-180	0%		0						
Construction of Temporary Jetty																
S14949	Prepare and Submit Method Statement for Construction of Temporary Jetty	P2-Cal.A	4	4	27-Apr-18	30-Apr-18	-151	0%		0						
S14951	Review and Discuss Method Statement for Construction of Temporary Jetty	P2-Cal.A	7	7	01-May-18	07-May-18	-151	0%		0						
S14953	Resubmit Method Statement for Construction of Temporary Jetty	P2-Cal.A	4	4	08-May-18	11-May-18	-151	0%		0						
S14955	Accept Method Statement for Construction of Temporary Jetty	P2-Cal.A	7	7	12-May-18	18-May-18	-151	0%		0						
Procurement of Major Material																
Civil/Structural																
S14981	Procurement and Delivery of Steel H-Pile	P2-Cal.A	800	390	31-Jan-17 A	14-May-19	-149	51.25%		-34						
S14983	Procurement and Delivery of ELS Waling & Struts Members	P2-Cal.A	1015	625	20-Jan-17 A	04-Jan-20	-39	38.42%		-65						
S14985	Offsite Fabrication of Pre-cast Seawall blocks	P2-Cal.A	40	40	27-Mar-18 A	29-May-18	-218	0%		-24						
S14987	Cast-in for sign gantry and Road Works	P2-Cal.A	120	120	10-Jul-18	06-Nov-18	398	0%		0						
S14995	Offsite Fabrication of Marine Survey Tower	P2-Cal.A	120	120	03-Jul-18	30-Oct-18	24	0%		0						
Subletting Package																
V Panel and Precast Concrete Panel																
S15160	V Panel and Precast Concrete Panel Award	P2-Cal.A	0	0	24-Apr-18	24-Apr-18	18	0%		0						
Installation of Socketed H-Pile (Reclaimed Section)																
S16381	Prepare Installation of Pre-bored Socketed H-Pile (Reclaimed Section) Tender for PM Acceptance	P2-Cal.A	7	3	16-Apr-18 A	14-Aug-18	-76	57.14%		-114						
ELS Works (Reclaimed Section)																
S16385	Prepare Excavation and ELS Works (Reclaimed Section) Tender Document for PM Acceptance	P2-Cal.A	7	3	07-Apr-18 A	22-Apr-18	37	57.14%		-9						
S16386	Invitation, Submission and Opening of Tender for Excavation and ELS Works (Reclaimed Section)	P2-Cal.A	14	14	23-Apr-18	06-May-18	37	0%		0						
S16387	Tender Interview and Recommendation to PM for Excavation and ELS Works (Reclaimed Section)	P2-Cal.A	21	21	07-May-18	27-May-18	37	0%		0						
S16388	Excavation and ELS Works (Reclaimed Section) Award	P2-Cal.A	0	0	27-May-18	27-May-18	37	0%		0						
Structural Works for Retaining Wall (Reclaimed Section)																
S16390	Invitation, Submission and Opening of Tender for Structural Works for Retaining Wall	P2-Cal.A	14	7	14-Mar-18 A	26-Apr-18	444	50%		-30						
S16391	Tender Interview and Recommendation to PM for Structural Works for Retaining Wall	P2-Cal.A	21	21	27-Apr-18	17-May-18	444	0%		0						
S16392	Structural Works for Retaining Wall Award	P2-Cal.A	0	0	17-May-18	17-May-18	444	0%		0						
Structural Works for U-Trough, Underpass and Abutment																
S16420	Invitation, Submission and Opening of Tender for Structural Works for U-Trough, Underpass and Abutment	P2-Cal.A	60	30	14-Mar-18 A	19-May-18	15	50%		-7						
S16440	Tender Interview and Recommendation to PM for Structural Works for U-Trough, Underpass and Abutment	P2-Cal.A	30	30	20-May-18	18-Jun-18	15	0%		0						
S16460	Structural Works for U-Trough, Underpass and Abutment Award	P2-Cal.A	0	0	18-Jun-18	18-Jun-18	15	0%		0						
Drainage and Sewerage Works (Existing Land) (At Grade Section)																
S17104	Submission and Opening of Tender for Drainage and Sewerage Works	P2-Cal.A	42	42	27-Apr-17 A	31-May-18	216	0%		-358						
S17106	Tender Interview and Recommendation to PM for Drainage and Sewerage Works	P2-Cal.A	21	21	01-Jun-18	21-Jun-18	216	0%		0						
S17108	Drainage and Sewerage Works Award	P2-Cal.A	0	0	21-Jun-18	21-Jun-18	216	0%		0						
Water Works (To be Incorporated in Irrigation Package)																
S17120	Prepare Water Works Tender Document for PM Acceptance	P2-Cal.A	30	5	07-Aug-17 A	24-Apr-18	265	83.33%		-231						
S17140	Submission and Opening of Tender for Water Works	P2-Cal.A	30	30	25-Apr-18	24-May-18	265	0%		0						

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)

Page :5 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance-BL1	2018									
											Apr	May	Jun	Jul	Aug					
S17160	Tender Interview and Recommendation to PM for Water Works	P2-Cal.A	21	21	25-May-18	14-Jun-18	265	0%		0										
S17180	Water Works Award	P2-Cal.A	0	0		14-Jun-18	265	0%		0										
Irrigation Works		P2-Cal.A	268	56	07-Aug-17 A	14-Jun-18	265			-44										
S17280	Prepare Irrigation Works Tender Document for PM Acceptance	P2-Cal.A	30	5	07-Aug-17 A	24-Apr-18	265	83.33%		-231										
S17300	Submission and Opening of Tender for Irrigation Works	P2-Cal.A	30	30	25-Apr-18	24-May-18	265	0%		0										
S17320	Tender Interview and Recommendation to PM for Irrigation Works	P2-Cal.A	21	21	25-May-18	14-Jun-18	265	0%		0										
S17340	Irrigation Works Award	P2-Cal.A	0	0		14-Jun-18	265	0%		0										
E & M Work (Electrical)		P2-Cal.A	27	9	15-Feb-18 A	28-Apr-18	80			-46										
S17410	Addendum for E & M Works (Electrical)	P2-Cal.A	21	9	15-Feb-18 A	28-Apr-18	80	57.14%		-52										
S17420	E & M Works (Electrical) Award	P2-Cal.A	0	0		28-Apr-18	80	0%		0										
E & M Works (MVAC)		P2-Cal.A	68	9	15-Feb-18 A	28-Apr-18	66			-5										
S17424-01	Addendum for E & M Works (MVAC)	P2-Cal.A	21	9	15-Feb-18 A	28-Apr-18	66	57.14%		-52										
S17425	E & M Works Award (MVAC)	P2-Cal.A	0	0		28-Apr-18	66	0%		0										
E & M Works (FS)		P2-Cal.A	38	9	15-Feb-18 A	28-Apr-18	80			-35										
S17428-01	Addendum for E & M Works (FS)	P2-Cal.A	21	9	15-Feb-18 A	28-Apr-18	80	57.14%		-52										
S17429	E & M Works (FS) Award	P2-Cal.A	0	0		28-Apr-18	80	0%		0										
E & M Works (Plumbing & Drainage)		P2-Cal.A	68	9	15-Feb-18 A	28-Apr-18	80			-5										
S17432-01	Addendum for E & M Works (Plumbing & Drainage)	P2-Cal.A	21	9	15-Feb-18 A	28-Apr-18	80	57.14%		-52										
S17433	E & M Works (Plumbing & Drainage) Award	P2-Cal.A	0	0		28-Apr-18	80	0%		0										
Section 3 of the Works All Works within Portion IV, V, VI, VII, VIII, and IX			430	202	25-Apr-17 A	07-Nov-18	173			-132										
Existing Land Section			365	149	25-Apr-17 A	15-Sep-18	226			-144										
Retaining Wall P2-A CH 500- 650			365	97	25-Apr-17 A	25-Jul-18	128			-92										
LC11926	Trial Pit of underground utilities	P2-Cal.C	6	4	12-Apr-18 A	24-Apr-18	160	33.33%		-5										
LC11929	CLP cable Diversion and relocation of WSD flowmeter chamber (by others) (NCE-029) (NCE-030) (PMI-027)	P2-Cal.A	365	5	25-Apr-17 A	24-Apr-18	65	98.63%		0										
LC11932	Removal of existing planter (NCE-019, EW-014, PMI-61 & CE-95)	P2-Cal.C	12	5	16-Apr-18 A	30-Apr-18	160	58.33%		-1										
Bay 1-2		P2-Cal.C	60	60	14-May-18	25-Jul-18	107			0										
LC11940	Pre-bore & Sheet Pile Installation of RW P2-A Bay 1 - 2 (RFI097)	P2-Cal.C	60	60	14-May-18	25-Jul-18	107	0%		0										
Bay 5-15		P2-Cal.C	72	72	25-Apr-18	21-Jul-18	83			0										
LC11961	ELS and Open Cut Excavation of RW P2-A Bay 5-15	P2-Cal.C	45	45	25-Apr-18	19-Jun-18	53	0%		0										
LC11962	Laying Blinding (RW P2-A Bay 5 - 15)	P2-Cal.C	7	7	20-Jun-18	27-Jun-18	53	0%		0										
LC11963	Construction of RW P2-A Base Slab - Bay 5 (Team C)	P2-Cal.C	10	10	28-Jun-18	10-Jul-18	53	0%		0										
LC11964	Construction of RW P2-A Wall Stem - Bay 5 (Team C)	P2-Cal.C	10	10	11-Jul-18	21-Jul-18	53	0%		0										
LC11967	Construction of RW P2-A Base Slab - Bay 7 (Team D)	P2-Cal.C	10	10	28-Jun-18	10-Jul-18	83	0%		0										
LC11968	Construction of RW P2-A Wall Stem - Bay 7 (Team D)	P2-Cal.C	10	10	11-Jul-18	21-Jul-18	83	0%		0										
P2 Road		P2-Cal.C	165	124	01-Dec-17 A	15-Sep-18	180			-69										
P2 CH 318 - 363		P2-Cal.C	88	88	01-Dec-17 A	04-Aug-18	-118			-110										
Foundation P2 CH318-363		P2-Cal.C	41	28	01-Dec-17 A	24-May-18	-118			-97										
LC12949-04	Relocation of Existing Pillar Box (EW070)	P2-Cal.C	30	1	01-Dec-17 A	20-Apr-18	-118	96.67%		-81										
LC12949-05	Lower Down Ground Level to +3.5mpd & UU Diversion	P2-Cal.C	40	27	06-Apr-18 A	24-May-18	-118	32.5%		0										
ELS P2 CH318-363 & SR2 CH100-110		P2-Cal.C	60	60	16-Apr-18 A	04-Aug-18	-118			-32										
LC12951	Overcome obstruction by Pre-bore method at CH318-363 (NCE072, NCE075 and CE067)	P2-Cal.C	60	58	16-Apr-18 A	02-Aug-18	-118	3.33%		-30										
LC12952	Installation of sheetpile wall at CH318-363	P2-Cal.C	60	60	25-May-18	04-Aug-18	-118	0%		0										
LC12957	Installation of Dewatering System and King Posts	P2-Cal.C	20	20	13-Jul-18	04-Aug-18	-118	0%		0										

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)

Page :6 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance-BL1	2018					
											Apr	May	Jun	Jul	Aug	
P2 CH 411- 500																
Structure P2 CH 411 - 500 (U Trough A)																
Wall Stem																
LC15110	Waterproofing of wall stem, backfill & removal of strut/wailing at Bay 6 & 7	P2-Cal.C	30	5	16-Mar-18 A	25-Apr-18	159	83.33%		-1	Waterproofing of wall stem, backfill & removal of strut/wailing at Bay 6 & 7					
LC15120	Waterproofing of wall stem, backfill & removal of strut/wailing at Bay 4 & 5	P2-Cal.C	30	18	19-Mar-18 A	11-May-18	159	40%		-12	Waterproofing of wall stem, backfill & removal of strut/wailing at Bay 4 & 5					
LC15130	Waterproofing of wall stem, backfill & removal of strut/wailing at Bay 2 & 3	P2-Cal.C	30	30	13-Apr-18 A	26-May-18	159	0%		-6	Waterproofing of wall stem, backfill & removal of strut/wailing at Bay 2 & 3					
LC15140	Waterproofing of wall stem, backfill & removal of strut/wailing at Bay 1	P2-Cal.C	30	30	02-May-18	06-Jun-18	189	0%		0	Waterproofing of wall stem, backfill & removal of strut/wailing at Bay 1					
LC15150	Construction of wall stem at Bay 6 & 7 - 2nd pour	P2-Cal.C	13	13	28-May-18	11-Jun-18	159	0%		0	Construction of wall stem at Bay 6 & 7 - 2nd pour					
LC15160	Construction of wall stem at Bay 4 & 5 - 2nd pour	P2-Cal.C	13	13	12-Jun-18	27-Jun-18	159	0%		0	Construction of wall stem at Bay 4 & 5 - 2nd pour					
LC15170	Construction of wall stem at Bay 2 & 3 - 2nd pour	P2-Cal.C	13	13	28-Jun-18	13-Jul-18	159	0%		0	Construction of wall stem at Bay 2 & 3 - 2nd pour					
LC15180	Construction of wall stem at Bay 1 - 2nd pour	P2-Cal.C	13	13	14-Jul-18	28-Jul-18	159	0%		0	Construction of wall stem at Bay 1 - 2nd pour					
LC15185	Waterproofing of wall stem, backfill & removal of strut/wailing at Bay 4 to 7	P2-Cal.C	30	30	28-Jun-18	02-Aug-18	185	0%		0	Waterproofing of wall stem, backfill & removal of strut/wailing at Bay 4 to 7					
LC15250	Construction of Drainage and Manhole	P2-Cal.C	60	42	06-Apr-18 A	15-Sep-18	180	30%		-76	Construction of Drainage and Manhole					
SR2																
Retaining Wall SR2-A & B CH250 - 310																
Retaining Wall SR2-B																
LC16592	Temporary Work Installation of RW P2-A Bay 1 - 3 (RF1105)	P2-Cal.C	45	22	10-Mar-18 A	16-May-18	166	51.11%		-8	Temporary Work Installation of RW P2-A Bay 1 - 3 (RF1105)					
LC16593	Excavation, Blinding & W/P of RW P2-A Bay 1 - 3 (RF1105)	P2-Cal.C	21	21	17-May-18	11-Jun-18	166	0%		0	Excavation, Blinding & W/P of RW P2-A Bay 1 - 3 (RF1105)					
LC16600	Construction of Base Slab (SR2-A & B Bay 1) (RF1105)	P2-Cal.C	15	15	12-Jun-18	29-Jun-18	166	0%		0	Construction of Base Slab (SR2-A & B Bay 1) (RF1105)					
LC16610	Construction of Base Slab (SR2-A & B Bay 2) (RF1105)	P2-Cal.C	15	15	30-Jun-18	18-Jul-18	166	0%		0	Construction of Base Slab (SR2-A & B Bay 2) (RF1105)					
LC16615	Construction of Base Slab (SR2-A & B Bay 3) (RF1105)	P2-Cal.C	15	15	19-Jul-18	04-Aug-18	166	0%		0	Construction of Base Slab (SR2-A & B Bay 3) (RF1105)					
SR2 CH170 - 250																
Structure SR2 CH 170 - 250 (U Trough A)																
LC17310	Construction of wall stem 1st pour (+3.0mpd) at CH182.5 - 194	P2-Cal.C	12	12	20-Apr-18	04-May-18	157	0%		0	Construction of wall stem 1st pour (+3.0mpd) at CH182.5 - 194					
LC17315	Construction of wall stem 1st pour (+3.0mpd) at CH208 - 222	P2-Cal.C	12	11	19-Apr-18 A	17-May-18	157	8.33%		-12	Construction of wall stem 1st pour (+3.0mpd) at CH208 - 222					
LC17320	Construction of wall stem 1st pour (+3.0mpd) at CH236 - 250	P2-Cal.C	12	12	20-Apr-18	04-May-18	158	0%		0	Construction of wall stem 1st pour (+3.0mpd) at CH236 - 250					
LC17330	Construction of wall stem 1st pour (+3.0mpd) at CH194 - 208	P2-Cal.C	12	2	06-Apr-18 A	19-May-18	157	83.33%		-25	Construction of wall stem 1st pour (+3.0mpd) at CH194 - 208					
LC17335	Construction of wall stem 1st pour (+3.0mpd) at CH222 - 236	P2-Cal.C	12	12	05-May-18	18-May-18	158	0%		0	Construction of wall stem 1st pour (+3.0mpd) at CH222 - 236					
LC17340	Waterproofing of wall stem, backfill & removal of strut/wailing at CH170 - 182.5	P2-Cal.C	10	10	21-May-18	01-Jun-18	157	0%		0	Waterproofing of wall stem, backfill & removal of strut/wailing at CH170 - 182.5					
LC17345	Waterproofing of wall stem, backfill & removal of strut/wailing at CH182.5 - 194	P2-Cal.C	10	10	02-Jun-18	13-Jun-18	157	0%		0	Waterproofing of wall stem, backfill & removal of strut/wailing at CH182.5 - 194					
LC17350	Waterproofing of wall stem, backfill & removal of strut/wailing at CH194 - 208	P2-Cal.C	10	10	14-Jun-18	26-Jun-18	157	0%		0	Waterproofing of wall stem, backfill & removal of strut/wailing at CH194 - 208					
LC17355	Waterproofing of wall stem, backfill & removal of strut/wailing at CH208 - 222	P2-Cal.C	10	10	27-Jun-18	09-Jul-18	157	0%		0	Waterproofing of wall stem, backfill & removal of strut/wailing at CH208 - 222					
LC17360	Waterproofing of wall stem, backfill & removal of strut/wailing at CH222 - 236	P2-Cal.C	10	10	10-Jul-18	20-Jul-18	157	0%		0	Waterproofing of wall stem, backfill & removal of strut/wailing at CH222 - 236					
Portion IV & VII																
Construction of DN2100 stormwater at Portion IV & VII																
Preboring																
Rig 1																
LC17666	Stage 9 -- Preboring for Dia. 2100 Drain Pipe (no.957-905)(52 nos.@ 2nos./d)(CE 041)	P2-Cal.C	26	26	01-Jun-18	03-Jul-18	-135	0%		0	Stage 9 -- Preboring for Dia. 2100 Drain Pipe (no.957-905)(52 nos.@ 2nos./d)(CE 041)					
LC17666-01	Stage 9 -- Preboring for Dia. 2100 Drain Pipe (no.958-1009)(52 nos.@ 2nos./d)(CE 041)	P2-Cal.C	26	26	07-Jun-18	09-Jul-18	-140	0%		0	Stage 9 -- Preboring for Dia. 2100 Drain Pipe (no.958-1009)(52 nos.@ 2nos./d)(CE 041)					
LC17666-02	Stage 9 -- Preboring for Dia. 2100 Drain Pipe (no.854-904)(50 nos.@ 2nos./d)(CE 041)	P2-Cal.C	25	25	21-May-18	20-Jun-18	-125	0%		0	Stage 9 -- Preboring for Dia. 2100 Drain Pipe (no.854-904)(50 nos.@ 2nos./d)(CE 041)					
LC17667	Stage 10 -- Pipe Pile Installation (79nos. @ 1.3nos./d)	P2-Cal.C	62	25	20-Mar-18 A	19-May-18	-125	59.68%		14	Stage 10 -- Pipe Pile Installation (79nos. @ 1.3nos./d)					
Rig 2																
LC17676	Stage 8 -- Preboring for Dia. 2100 Drain Pipe (no.1010-1130)(120nos.@ 2.4nos./d)(CE 041)	P2-Cal.C	50	39	16-Apr-18 A	06-Jun-18	-140	22%		7	Stage 8 -- Preboring for Dia. 2100 Drain Pipe (no.1010-1130)(120nos.@ 2.4nos./d)(CE 041)					

— Primary Baseline — Critical Remaining Work
— Actual Work ◆ Milestone
— Remaining Work — Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)

Page :7 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance - BL1	2018							
											Apr	May	Jun	Jul	Aug			
Rig 3		P2-Cal.C	45	34	23-Mar-18 A	31-May-18	-135			-9								
LC17677-2	Stage 7 -- Preboring for Dia. 2100 Drain Pipe (no. 763-853)(90 nos.@ 2nos./d)(CE 041)	P2-Cal.C	45	34	23-Mar-18 A	31-May-18	-135	24.44%		-9								
ELS		P2-Cal.C	61	61	03-May-18	16-Jul-18	-140			0								
Installation Sheet Pile - 24m		P2-Cal.C	61	61	03-May-18	16-Jul-18	-140			0								
LC17686	Stage 7 -- Sheet Pile installation 24m length for SMH9105 - 9104 (83 nos.@15pcs./d)	P2-Cal.C	6	6	03-May-18	09-May-18	-85	0%		0								
LC17686-01	Stage 7 -- Sheet Pile installation 24m length for SMH9104 - 9103 (125 nos.@15pcs./d)	P2-Cal.C	9	9	01-Jun-18	11-Jun-18	-116	0%		0								
LC17687	Stage 8 -- Sheet Pile installation 24m length for SMH9110 - 9109 (105 nos.@15pcs./d)	P2-Cal.C	7	7	16-May-18	24-May-18	-97	0%		0								
LC17687-01	Stage 8 -- Sheet Pile installation 24m length for SMH9109 - 9108 (105 nos.@15pcs./d)	P2-Cal.C	7	7	07-Jun-18	14-Jun-18	-115	0%		0								
LC17687-02	Stage 9 -- Sheet Pile installation 24m length for SMH9108 - 9107 (90 nos.@15pcs./d)	P2-Cal.C	6	6	10-Jul-18	16-Jul-18	-140	0%		0								
LC17688	Stage 9 -- Sheet Pile installation 24m length for SMH9107 - 9106 (95 nos.@15pcs./d)	P2-Cal.C	6	6	10-Jul-18	16-Jul-18	-140	0%		0								
Drainage works		P2-Cal.C	89	89	02-May-18	16-Aug-18	-126			0								
SMH9103-SMH9104		P2-Cal.C	33	33	12-Jun-18	21-Jul-18	-116			0								
LC17690	Trench Excavation and Strut Installation for Construction of Dia. 2100 Drain Pipe (SMH9103 to SMH9104)	P2-Cal.C	10	10	12-Jun-18	23-Jun-18	-116	0%		0								
LC17690-2	Bedding And Inspection	P2-Cal.C	3	3	25-Jun-18	27-Jun-18	-116	0%		0								
LC17690-3	Manhole construction and Pipe Laying (SMH9103 and SMH9104)	P2-Cal.C	20	20	28-Jun-18	21-Jul-18	-116	0%		0								
SMH9104-SMH9105		P2-Cal.C	41	41	10-May-18	28-Jun-18	-85			0								
LC17691	Trench Excavation and Strut Installation for Construction of Dia. 2100 Drain Pipe (SMH9104 to SMH9105)	P2-Cal.C	10	10	10-May-18	21-May-18	-85	0%		0								
LC17691-2	Bedding And Inspection	P2-Cal.C	3	3	23-May-18	25-May-18	-85	0%		0								
LC17691-3	Manhole construction and Pipe Laying (SMH9105)	P2-Cal.C	16	16	26-May-18	13-Jun-18	-85	0%		0								
LC17691-5	Inspection & Backfill	P2-Cal.C	14	14	12-Jun-18	28-Jun-18	-85	0%		0								
SMH9105-SMH9106		P2-Cal.C	41	41	21-May-18	10-Jul-18	-94			0								
LC17692	Trench Excavation and Strut Installation for Construction of Dia. 2100 Drain Pipe (SMH9105 to SMH9106)	P2-Cal.C	10	10	21-May-18	01-Jun-18	-94	0%		0								
LC17692-2	Bedding And Inspection	P2-Cal.C	3	3	02-Jun-18	05-Jun-18	-94	0%		0								
LC17692-3	Manhole construction and Pipe Laying (SMH9106)	P2-Cal.C	16	16	06-Jun-18	25-Jun-18	-94	0%		0								
LC17692-5	Inspection & Backfill	P2-Cal.C	14	14	23-Jun-18	10-Jul-18	-94	0%		0								
SMH9106-SMH9107		P2-Cal.C	10	10	17-Jul-18	27-Jul-18	-140			0								
LC17693	Trench Excavation and Strut Installation for Construction of Dia. 2100 Drain Pipe (SMH9106 to SMH9107)	P2-Cal.C	10	10	17-Jul-18	27-Jul-18	-140	0%		0								
SMH9107-SMH9108		P2-Cal.C	10	10	17-Jul-18	27-Jul-18	-140			0								
LC17694	Trench Excavation and Strut Installation for Construction of Dia. 2100 Drain Pipe (SMH9107 to SMH9108)	P2-Cal.C	10	10	17-Jul-18	27-Jul-18	-140	0%		0								
SMH9108-SMH9109		P2-Cal.C	41	41	15-Jun-18	03-Aug-18	-115			0								
LC17699	Trench Excavation and Strut Installation for Construction of Dia. 2100 Drain Pipe (SMH9108 to SMH9109)	P2-Cal.C	10	10	15-Jun-18	27-Jun-18	-115	0%		0								
LC17701	Bedding And Inspection	P2-Cal.C	3	3	28-Jun-18	30-Jun-18	-115	0%		0								
LC17702	Manhole construction and Pipe Laying (SMH9109)	P2-Cal.C	16	16	03-Jul-18	20-Jul-18	-115	0%		0								
LC17704	Inspection & Backfill	P2-Cal.C	14	14	19-Jul-18	03-Aug-18	-115	0%		0								
SMH9109-SMH9110		P2-Cal.C	41	41	25-May-18	13-Jul-18	-97			0								
LC17705	Trench Excavation and Strut Installation for Construction of Dia. 2100 Drain Pipe (SMH9109-9110)	P2-Cal.C	10	10	25-May-18	05-Jun-18	-97	0%		0								
LC17707	Bedding And Inspection	P2-Cal.C	3	3	06-Jun-18	08-Jun-18	-97	0%		0								
LC17708	Manhole construction and Pipe Laying (SMH9110)	P2-Cal.C	16	16	09-Jun-18	28-Jun-18	-97	0%		0								
LC17710	Inspection & Backfill	P2-Cal.C	14	14	27-Jun-18	13-Jul-18	-97	0%		0								
SMH9110-Outfall		P2-Cal.C	89	89	02-May-18	16-Aug-18	-126			0								
LC17711	Fabrication of Precast Outfall	P2-Cal.C	21	21	02-May-18	26-May-18	-126	0%		0								
LC17712	Removal of Existing Seawall and Trench Excavation	P2-Cal.C	21	21	28-May-18	21-Jun-18	-126	0%		0								
LC17713	Bedding And Inspection	P2-Cal.C	3	3	22-Jun-18	25-Jun-18	-126	0%		0								

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)

Page :8 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance - BL1	2018									
											Apr	May	Jun	Jul	Aug					
LC17714	Installation of Precast Outfall	P2-Cal.C	5	5	26-Jun-18	30-Jun-18	-126	0%		0										
LC17715	Lay Dia. 2100 Drainage for Existing Outfalls along Existing Seawall (SMH9110- Outfall) (63m)	P2-Cal.C	10	10	03-Jul-18	13-Jul-18	-126	0%		0										
LC17716	Reinstatement of Seawall and Backfilling Works	P2-Cal.C	30	30	13-Jul-18	16-Aug-18	-126	0%		0										
New Reclaimed Section			396	202	14-Nov-17 A	07-Nov-18	24			37										
Marine Works			396	202	14-Nov-17 A	07-Nov-18	24			37										
Initial Works			60	60	20-Apr-18	03-Jul-18	74			0										
MC10060	Installation of Piezometer/ O Well/ Extensometer (Type RB)	P2-Cal.C	7	7	05-May-18	12-May-18	-91	0%		0										
MC10070	Baseline for Piezometer/ O Well/ Extensometer (Type RB)	P2-Cal.C	10	10	14-May-18	25-May-18	-91	0%		0										
MC10156	Installation of Type 2 Settlement Marker (Type RA)	P2-Cal.C	7	7	20-Apr-18	27-Apr-18	-84	0%		0										
MC10160	Baseline for Type 2 Settlement Marker (Type RA)	P2-Cal.C	3	3	28-Apr-18	02-May-18	-84	0%		0										
MC10170	Installation of Type 2 Settlement Marker (Type RB)	P2-Cal.C	7	7	05-May-18	12-May-18	11	0%		0										
MC10175	Baseline for Type 2 Settlement Marker (Type RB)	P2-Cal.C	3	3	14-May-18	16-May-18	11	0%		0										
Steel Cofferdam and Water Gate			60	60	20-Apr-18	03-Jul-18	74			0										
Steel Cofferdam Installation			60	60	20-Apr-18	03-Jul-18	74			0										
Reinstatement works			60	60	20-Apr-18	03-Jul-18	74			0										
Type 1			60	60	20-Apr-18	03-Jul-18	74			0										
Removal of S/P at transition zone			60	60	20-Apr-18	03-Jul-18	74			0										
MC10304-02	Removal of Underwater S/P	P2-Cal.C	60	60	20-Apr-18	03-Jul-18	74	0%		0										
Dredging Work			146	71	14-Nov-17 A	16-Jul-18	-133			-50										
MC10580	Dredge CH125-150 (Bottom) (2472m3) (NCE099)	P2-Cal.C	2	2	10-Mar-18 A	21-Apr-18	-183	0%		-31										
MC10615	Dredge CH150-200 (Bottom) (4672m3)	P2-Cal.C	2	1	03-Mar-18 A	23-Apr-18	-180	50%		-38										
MC10635	Dredge CH250-300 (Upper) (28432m3)	P2-Cal.C	16	1	14-Nov-17 A	24-Apr-18	-177	93.75%		-113										
MC10655	Dredge CH200-250 (Bottom) (6363m3)	P2-Cal.C	3	3	25-Apr-18	27-Apr-18	-177	0%		0										
MC10675	Dredge CH300-350 (Upper) (26655m3)	P2-Cal.C	15	2	23-Nov-17 A	30-Apr-18	-172	86.67%		-111										
MC10695	Dredge CH250-300 (Bottom) (6504m3)	P2-Cal.C	3	3	02-May-18	04-May-18	-172	0%		0										
MC10715	Dredge CH350-400 (Upper) (30209m3)	P2-Cal.C	17	2	18-Nov-17 A	07-May-18	-156	88.24%		-118										
MC10735	Dredge CH300-350 (Bottom) (6910m3)	P2-Cal.C	3	3	08-May-18	10-May-18	-156	0%		0										
MC10755	Dredge CH400-450 (Upper) (40871m3)	P2-Cal.C	23	4	21-Dec-17 A	15-May-18	-151	82.61%		-91										
MC10775	Dredge CH350-400 (Bottom) (7794m3)	P2-Cal.C	4	4	16-May-18	19-May-18	-151	0%		0										
MC10795	Dredge CH450-500 (Upper) (71080m3)	P2-Cal.C	40	5	29-Nov-17 A	26-May-18	-148	87.5%		-102										
MC10815	Dredge CH400-450 (Bottom) (10120m3)	P2-Cal.C	5	5	28-May-18	01-Jun-18	-148	0%		0										
MC10835	Dredge CH500-560 (Upper) (14452m3)	P2-Cal.C	13	9	12-Dec-17 A	12-Jun-18	-133	30.77%		-132										
MC10845	Dredge CH450-560 (Middle) for treatment (7500m3)	P2-Cal.C	15	15	13-Jun-18	30-Jun-18	-133	0%		0										
MC10855	Dredge CH450-560 (Bottom) for treatment (6000m3) and to be stored at barge (19000m3)	P2-Cal.C	12	12	03-Jul-18	16-Jul-18	-133	0%		0										
Bathymetric and Seismic Survey			71	71	11-Apr-18 A	18-Jul-18	-133			-10										
MC10895	Survey CH100-150	P2-Cal.C	2	2	11-Apr-18 A	24-Apr-18	-183	0%		-10										
MC10915	Survey CH150-200	P2-Cal.C	2	2	25-Apr-18	26-Apr-18	-181	0%		0										
MC10935	Survey CH200-250	P2-Cal.C	2	2	28-Apr-18	30-Apr-18	-177	0%		0										
MC10955	Survey CH250-300	P2-Cal.C	2	2	05-May-18	07-May-18	-172	0%		0										
MC10975	Survey CH300-350	P2-Cal.C	2	2	11-May-18	12-May-18	-156	0%		0										
MC10995	Survey CH350-400	P2-Cal.C	2	2	21-May-18	23-May-18	-151	0%		0										
MC11015	Survey CH400-450	P2-Cal.C	2	2	02-Jun-18	04-Jun-18	-148	0%		0										
MC11035	Survey CH450-560	P2-Cal.C	2	2	17-Jul-18	18-Jul-18	-133	0%		0										

█ Primary Baseline █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work ▼ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)
Page :9 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance-BL1	2018																			
											Apr	May	Jun	Jul	Aug															
Filling of Recycle G400 Rock at Dredged Trench																														
MC11055	Fill of Recycle G400 at CH75-112 (7237m3)	P2-Cal.C	4	4	25-Apr-18	28-Apr-18	-183	0%	0	0																				
MC11075	Diven S/P from CH200 to 250 as Jetty	P2-Cal.C	10	10	02-May-18	12-May-18	-164	0%	0	0																				
MC11085	Fill Recycle G400 at CH112-162 (12707m3)	P2-Cal.C	7	7	30-Apr-18	08-May-18	-183	0%	0	0																				
MC11105	Fill Recycle G400 at CH162-212 (20761m3)	P2-Cal.C	10	10	09-May-18	19-May-18	-183	0%	0	0																				
MC11125	Fill Recycle G400 at CH212-262 (21729m3)	P2-Cal.C	13	13	21-May-18	05-Jun-18	-183	0%	0	0																				
MC11145	Fill Recycle G400 at CH262-312 (22016m3)	P2-Cal.C	13	13	06-Jun-18	21-Jun-18	-175	0%	0	0																				
MC11165	Fill Recycle G400 at CH312-362 (22354m3)	P2-Cal.C	13	13	22-Jun-18	07-Jul-18	-175	0%	0	0																				
MC11185	Fill Recycle G400 at CH362-412 (25473m3)	P2-Cal.C	12	12	09-Jul-18	21-Jul-18	-175	0%	0	0																				
Construction of Seawall Foundation (Dredged Area)																														
Laying of Type A Rockfill (Base)																														
MC11265	Type A Rockfill CH213-262 (797m3)	P2-Cal.C	1	1	06-Jun-18	06-Jun-18	-183	0%	0	0																				
MC11275	Type A Rockfill CH262-312 (952m3)	P2-Cal.C	2	2	22-Jun-18	23-Jun-18	-169	0%	0	0																				
MC11285	Type A Rockfill CH312-362 (860m3)	P2-Cal.C	1	1	09-Jul-18	09-Jul-18	-175	0%	0	0																				
Laying of Geotextile Type A (Base)																														
MC11325	Geotextile Type A CH75-112 (801m2)	P2-Cal.C	1	1	30-Apr-18	30-Apr-18	-177	0%	0	0																				
MC11335	Geotextile Type A CH112-162 (889m2)	P2-Cal.C	1	1	09-May-18	09-May-18	-182	0%	0	0																				
MC11345	Geotextile Type A CH162-212 (915m2)	P2-Cal.C	1	1	21-May-18	21-May-18	-175	0%	0	0																				
MC11355	Geotextile Type A CH212-262 (929m2)	P2-Cal.C	1	1	07-Jun-18	07-Jun-18	-183	0%	0	0																				
MC11365	Geotextile Type A CH262-312 (1023m2)	P2-Cal.C	1	1	25-Jun-18	25-Jun-18	-169	0%	0	0																				
MC11375	Geotextile Type A CH312-362 (952m2)	P2-Cal.C	1	1	10-Jul-18	10-Jul-18	-175	0%	0	0																				
Laying of Granular Filter (Base)																														
MC11415	Granular Filter CH75-112 (1382m3)	P2-Cal.C	2	2	02-May-18	03-May-18	-177	0%	0	0																				
MC11425	Granular Filter CH112-162 (2051m3)	P2-Cal.C	3	3	10-May-18	12-May-18	-182	0%	0	0																				
MC11435	Granular Filter CH162-212 (2219m3)	P2-Cal.C	3	3	23-May-18	25-May-18	-175	0%	0	0																				
MC11445	Granular Filter CH212-262 (1665m3)	P2-Cal.C	2	2	08-Jun-18	09-Jun-18	-183	0%	0	0																				
MC11455	Granular Filter CH262-312 (1217m3)	P2-Cal.C	2	2	26-Jun-18	27-Jun-18	-169	0%	0	0																				
MC11465	Granular Filter CH312-362 (852m3)	P2-Cal.C	1	1	11-Jul-18	11-Jul-18	-175	0%	0	0																				
Laying Geotextile Type A (Ground Treatment)																														
MC12005	Geotextile Type A (No-Dredged Area) - 2 layers CH40-95 (2913m2)	P2-Cal.C	3	2	14-Apr-18 A	21-Apr-18	-165	33.33%	0	-4																				
MC12015	Geotextile Type A (Dredged Area) and Granular Filter CH95-162 (1292m2)	P2-Cal.C	3	3	14-May-18	16-May-18	-182	0%	0	0																				
MC12025	Geotextile Type A (Dredged Area) and Granular Filter CH162-212 (1400m2)	P2-Cal.C	3	3	26-May-18	29-May-18	-175	0%	0	0																				
MC12035	Geotextile Type A (Dredged Area) and Granular Filter CH212-CH262 (1796m2)	P2-Cal.C	3	3	11-Jun-18	13-Jun-18	-183	0%	0	0																				
MC12045	Geotextile Type A (No-Dredged Area) CH262-312 (2426m2)	P2-Cal.C	4	4	28-Jun-18	03-Jul-18	-169	0%	0	0																				
MC12055	Geotextile Type A (No-Dredged Area) CH312-362 (2606m2)	P2-Cal.C	4	4	12-Jul-18	16-Jul-18	-175	0%	0	0																				
Placing Sand Blanket (Non-Dredged Area)																														
MC12105	Sand Blanket CH225-275 (1205m3)	P2-Cal.C	3	3	30-Jun-18	04-Jul-18	-169	0%	0	0																				
MC12115	Sand Blanket CH275-325 (2316m3)	P2-Cal.C	5	5	14-Jul-18	19-Jul-18	-175	0%	0	0																				
Installation of Band Drain (Non-Dredged Area)																														
MC12163	Band Drain CH38-75 (1130nos)	P2-Cal.C	12	12	05-May-18	18-May-18	-136	0%	0	0																				
MC12165	Band Drain CH75-95 (380nos)	P2-Cal.C	4	4	16-Jul-18	19-Jul-18	-182	0%	0	0																				
Filling of Reclamation Fill to Seabed Level																														
MC12335	Reclamation Fill CH95-125 (5480m3)	P2-Cal.C	4	4	17-May-18	21-May-18	-182	0%	0	0																				

— Primary Baseline ■ Critical Remaining Work
■ Actual Work ◆ Milestone
■ Remaining Work ▶ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)
Page :10 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance - BL1	2018						
											Apr	May	Jun	Jul	Aug		
MC12345	Reclamation Fill CH125-175 (6281m3)	P2-Cal.C	5	5	30-May-18	04-Jun-18	-175	0%	0	0							
MC12355	Reclamation Fill CH175-225 (8443m3)	P2-Cal.C	6	6	14-Jun-18	21-Jun-18	-183	0%	0	0							
Laying of Geotextile Type A on Top of Reclamation Fill		P2-Cal.C	26	26	23-May-18	22-Jun-18	-183			0							
MC12415	Geotextile Type A CH80-115 (437m2)	P2-Cal.C	1	1	23-May-18	23-May-18	-182	0%	0	0							
MC12425	Geotextile Type A CH115-165 (683m2)	P2-Cal.C	1	1	05-Jun-18	05-Jun-18	-171	0%	0	0							
MC12435	Geotextile Type A CH165-215 (784m2)	P2-Cal.C	1	1	22-Jun-18	22-Jun-18	-183	0%	0	0							
Construction of Eastern Seawall Up to +2.5mPD		P2-Cal.C	36	36	24-May-18	06-Jul-18	-182			0							
Filling of G400 Rock as East Seawall Core (+2.5mPD)		P2-Cal.C	28	28	24-May-18	26-Jun-18	-183			0							
MC11505	Fill G400 at CH80-115 (2508m3) for Vectrical Seawall	P2-Cal.C	2	2	24-May-18	25-May-18	-182	0%	0	0							
MC11510	Construction of temporary 1500 dia. drain pipe (CH70 - 110)	P2-Cal.C	9	9	26-May-18	05-Jun-18	-182	0%	0	0							
MC11515	Fill G400 at CH115-165 (3900m3) for Vectrical Seawall	P2-Cal.C	2	2	06-Jun-18	07-Jun-18	-171	0%	0	0							
MC11525	Fill G400 at CH165-215 (5826m3) for Vectrical Seawall	P2-Cal.C	3	3	23-Jun-18	26-Jun-18	-183	0%	0	0							
Laying of Type A Rockfill as East Seawall Core (+2.5mPD)		P2-Cal.C	8	8	23-Jun-18	03-Jul-18	-182			0							
MC11605	Type A Rockfill CH80-115 (2023m3) After Vectrical Seawall Completion	P2-Cal.C	4	4	23-Jun-18	27-Jun-18	-182	0%	0	0							
MC11615	Type A Rockfill CH115-165 (2880m3) After Vectrical Seawall Completion	P2-Cal.C	4	4	28-Jun-18	03-Jul-18	-182	0%	0	0							
Laying of Geotextile Type A as East Seawall Core (+2.5mPD)		P2-Cal.C	5	5	28-Jun-18	04-Jul-18	-182			0							
MC11705	Geotextile Type A CH80-115 (757m2)	P2-Cal.C	1	1	28-Jun-18	28-Jun-18	-179	0%	0	0							
MC11715	Geotextile Type A CH115-165 (1138m2)	P2-Cal.C	1	1	04-Jul-18	04-Jul-18	-182	0%	0	0							
Laying of Granular Filter as East Seawall Core (+2.5mPD)		P2-Cal.C	6	6	29-Jun-18	06-Jul-18	-182			0							
MC11805	Granular Filter CH80-115 (739m3)	P2-Cal.C	1	1	29-Jun-18	29-Jun-18	-179	0%	0	0							
MC11815	Granular Filter CH115-165 (1061m3)	P2-Cal.C	2	2	05-Jul-18	06-Jul-18	-182	0%	0	0							
Construction of Vertical Seawall		P2-Cal.C	43	43	06-Jun-18	27-Jul-18	-183			0							
Construction of Vertical Seawall (Type 2 & 3)		P2-Cal.C	14	14	06-Jun-18	22-Jun-18	-182			0							
MC11905	Installation of guidance rail for leveling stone	P2-Cal.C	2	2	06-Jun-18	07-Jun-18	-182	0%	0	0							
MC11915	Seawall (Type 2 & 3) Laying of leveling stone Type 2 & 3	P2-Cal.C	3	3	08-Jun-18	11-Jun-18	-182	0%	0	0							
MC11925	Seawall (Type 2 & 3) Laying of M9 (18 nos)	P2-Cal.C	2	2	12-Jun-18	13-Jun-18	-182	0%	0	0							
MC11935	Seawall (Type 2 & 3) Laying 1st Layer (39 nos)	P2-Cal.C	4	4	14-Jun-18	19-Jun-18	-182	0%	0	0							
MC11945	Seawall (Type 2 & 3) Laying 2nd Layer (32 nos)	P2-Cal.C	3	3	20-Jun-18	22-Jun-18	-182	0%	0	0							
Construction of Vertical Seawall (Type 1 & 4)		P2-Cal.C	26	26	27-Jun-18	27-Jul-18	-183			0							
MC11955	Installation of guidance rail for leveling stone	P2-Cal.C	2	2	27-Jun-18	28-Jun-18	-183	0%	0	0							
MC11965	Seawall (Type 1 & 4) Laying of leveling stone Type 1 & 4	P2-Cal.C	5	5	29-Jun-18	05-Jul-18	-183	0%	0	0							
MC11975	Seawall (Type 1 & 4) Laying of M9 (65 nos)	P2-Cal.C	7	7	06-Jul-18	13-Jul-18	-183	0%	0	0							
MC11985	Seawall (Type 1 & 4) Laying 1st Layer (124 nos)	P2-Cal.C	12	12	14-Jul-18	27-Jul-18	-183	0%	0	0							
Filling of Reclamation Fill to -2.0mPD		P2-Cal.C	64	64	23-Apr-18	10-Jul-18	-182			0							
MC12653	Reclamation Fill to -2.0mPD CH0-40 (2113m3) - Sandfill	P2-Cal.C	2	2	23-Apr-18	24-Apr-18	-136	0%	0	0							
MC12655	Reclamation Fill to -2.0mPD CH40-80 (3435m3) - Sandfill	P2-Cal.C	2	2	25-Apr-18	26-Apr-18	-136	0%	0	0							
MC12655-01	Construction of temporary 1500 dia. drain pipe (CH30 - 70)	P2-Cal.C	7	7	30-Apr-18	08-May-18	-134	0%	0	0							
MC12665	Reclamation Fill to -2.0mPD CH80-155 (4382m3)	P2-Cal.C	3	3	07-Jul-18	10-Jul-18	-182	0%	0	0							
Filling of Reclamation Fill -2.0 to +2.5mPD		P2-Cal.C	66	66	25-Apr-18	14-Jul-18	-182			0							
MC12883	Reclamation Fill to +2.5mPD CH0-40 (7413m3) - Sandfill	P2-Cal.C	4	4	25-Apr-18	28-Apr-18	-132	0%	0	0							
MC12885	Reclamation Fill to +2.5mPD CH40-80 (10195m3) - Sandfill	P2-Cal.C	6	6	27-Apr-18	04-May-18	-136	0%	0	0							
MC12890	Construction of temporary 1500 dia. drain pipe (CH0 - 30)	P2-Cal.C	5	5	09-May-18	14-May-18	-134	0%	0	0							
MC12895	Reclamation Fill to +2.5mPD CH80-150 (8362m3)	P2-Cal.C	4	4	11-Jul-18	14-Jul-18	-182	0%	0	0							

Primary Baseline
 Critical Remaining Work
 Actual Work
◆ Milestone
 Remaining Work
 Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)
Page :11 of 12

Date	Revision	Checked	Approved
20-Apr-18			

Activity ID	Activity Name	Calendar	Original Duration	Remaining Duration	Start	Finish	Total Float	Activity % Complete	TRA	Variance - BL1	2018				
											Apr	May	Jun	Jul	Aug
Filling of Compacted Fill +2.5 to +5.5mPD															
MC12950	Compacted Fill to +5.5mPD CH0-40 (5773m3)	P2-Cal.C	6	6	19-May-18	26-May-18	-132	0%	0	0					
Surcharge															
Placing Surcharge															
MC13015	Placing Surcharge Area 1a (CH0-30) (2990m3)	P2-Cal.C	3	3	28-May-18	30-May-18	-123	0%	0	0					
Surcharging															
MC13155	Surcharge Area 1a (CH0-30) (2990m3)	P2-Cal.A	120	120	31-May-18	27-Sep-18	-158	0%	0	0					
Full-scale Treatment of Cement S/S of Marine Sediment															
MC14075	Treatment	P2-Cal.C	250	89	06-Jan-18 A	30-Aug-18	-164	64.4%	58	65					
MC14080	Curing, Stockpiling and Filling	P2-Cal.C	313	145	06-Jan-18 A	07-Nov-18	16	53.67%	65	65					
Modification Works of Existing Seawall															
MC14145	Excavation and Removal of existing seawall	P2-Cal.C	15	15	29-Jun-18	17-Jul-18	95	0%	0	0					
MC14165	Excavation down to -0.5mPD	P2-Cal.C	20	20	18-Jul-18	09-Aug-18	95	0%	0	0					
Section 4 of the Works - Preservation and Protection of Existing Trees															
LC25260	Preservation and Protection of Existing Trees	P2-Cal.A	1451	1109	12-Jan-17 A	05-May-21	-221	23.57%	-124	-124					
LC25280	Nursery Transplanted Trees at the Contractor's holding nursery	P2-Cal.A	1177	1011	28-Apr-17 A	24-Jan-21	-120	14.1%	-191	-191					

- █ Primary Baseline
- █ Critical Remaining Work
- █ Actual Work
- █ Remaining Work
- ◆ Milestone
- ▾ Summary

NE/2015/02 Tseung Kwan O - Lam Tin Tunnel-Road P2 and Associated Works (Apr-18)

3 Monthly Rolling Programme
(Data Date : 20-Apr-2018)
Page :12 of 12

Date	Revision	Checked	Approved
20-Apr-18			

NE/2017/02 - Updated Programme (April 2018)

Activity ID	Activity Name	Original Duration	Calendar	Activity % Complete	Remaining Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Float	Time Risk Allowance	2018												2019												2020												2021												
														Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
NE/2017/02 - Updated Programme (April 2018)														1471																																																
Contractual Dates														1461																																																
Commencement Date														0																																																
K10000	Contract Date	0	7d	100%	0	20-Nov-17 A	30-Nov-17 A	08-Apr-18	29-Nov-21	08-Apr-18	29-Nov-21	08-Apr-18	29-Nov-21	0																																																
K10010	Starting Date	0	7d	100%	0	30-Nov-17 A		08-Apr-18		08-Apr-18				0																																																
Key Dates (contract)														195																																																
K10020	Key Date 1 - Completion of works for the T&C of route-wide lighting, E&M and TCSS	0	7d	0%	0	18-May-20	29-Nov-20	18-May-20	29-Nov-20	18-May-20	29-Nov-20	18-May-20	29-Nov-20	0																																																
K10030	Key Date 2 - Completion of works for the opening of Road P2	0	7d	0%	0		29-Nov-20*		29-Nov-20		29-Nov-20		29-Nov-20	0																																																
Key Dates (planned)														196																																																
K10040	Key Date 1 - Completion of works for the T&C of route-wide lighting, E&M and TCSS (planned)	0	7d	0%	0	16-May-20	28-Nov-20	16-May-20	28-Nov-20	16-May-20	28-Nov-20	16-May-20	28-Nov-20	1																																																
K10050	Key Date 2 - Completion of works for the opening of Road P2 (planned)	0	7d	0%	0		28-Nov-20*		28-Nov-20		28-Nov-20		29-Nov-20	1																																																
Completion Dates (contract)														1190																																																
K10060	Section 1 - All works not covered by other Sections	0	7d	0%	0	01-Aug-20*	01-Aug-20*	01-Aug-20	01-Aug-20	01-Aug-20	01-Aug-20	01-Aug-20	01-Aug-20	0																																																
K10070	Section 2 - Bridgeworks	0	7d	0%	0	29-Nov-20*	29-Nov-20*	29-Nov-20	29-Nov-20	29-Nov-20	29-Nov-20	29-Nov-20	29-Nov-20	0																																																
K10080	Section 3 - Preservation and Protection of Existing Trees	0	7d	0%	0	29-Nov-20*	29-Nov-20*	29-Nov-20	29-Nov-20	29-Nov-20	29-Nov-20	29-Nov-20	29-Nov-20	0																																																
K10090	Section 4 - Landscape Softworks	0	7d	0%	0	29-Nov-20*	29-Nov-20*	29-Nov-20	29-Nov-20	29-Nov-20	29-Nov-20	29-Nov-20	29-Nov-20	0																																																
K10100	Section 5 - Establishment Works	0	7d	0%	0	29-Nov-21*	29-Nov-21*	29-Nov-21	29-Nov-21	29-Nov-21	29-Nov-21	29-Nov-21	29-Nov-21	0																																																
K10110	Section 6 - Community Liaison Centre	0	7d	0%	0	27-Aug-18*	27-Aug-18*	27-Aug-18	27-Aug-18	27-Aug-18	27-Aug-18	27-Aug-18	27-Aug-18	0																																																
Completion Dates (planned)														1182																																																
K10120	Section 1 - All works not covered by other Sections (planned)	0	7d	0%	0	29-Jul-20*	29-Jul-20*	29-Jul-20	29-Jul-20	29-Jul-20	29-Jul-20	29-Jul-20	29-Jul-20	3																																																
K10130	Section 2 - Bridgeworks (planned)	0	7d	0%	0	28-Nov-20*	28-Nov-20*	28-Nov-20	28-Nov-20	28-Nov-20	28-Nov-20	28-Nov-20	28-Nov-20	1																																																
K10140	Section 3 - Preservation and Protection of Existing Trees (planned)	0	7d	0%	0	28-Nov-20*	28-Nov-20*	28-Nov-20	28-Nov-20	28-Nov-20	28-Nov-20	28-Nov-20	28-Nov-20	1																																																
K10150	Section 4 - Landscape Softworks (planned)	0	7d	0%	0	21-Nov-20*	21-Nov-20*	21-Nov-20	21-Nov-20	21-Nov-20	21-Nov-20	21-Nov-20	21-Nov-20	8																																																
K10160	Section 5 - Establishment Works (planned)	0	7d	0%	0	21-Nov-21*	21-Nov-21*	21-Nov-21	21-Nov-21	21-Nov-21	21-Nov-21	21-Nov-21	21-Nov-21	8																																																
K10170	Section 6 - Community Liaison Centre (planned)	0	7d	0%	0	27-Aug-18*	27-Aug-18*	27-Aug-18	27-Aug-18	27-Aug-18	27-Aug-18	27-Aug-18	27-Aug-18	0																																																
Access Dates														477																																																
K10180	Portion I	0	6d	100%	0	17-Nov-17 A	21-Sep-19	08-Apr-18	21-Sep-19	21-Sep-19	21-Sep-19	29-Nov-21	650																																																	
K10190	Portion II	0	6d	100%	0	30-Nov-17 A		08-Apr-18		29-Nov-21				0																																																
K10200	Portion III	0	6d	100%	0	17-Nov-17 A		08-Apr-18		29-Nov-21				0																																																
K10210	Portion IV	0	6d	100%	0	21-Sep-19*		21-Sep-19		21-Sep-19				0																																																
K10220	Portion V	0	6d	100%	0	30-Nov-17 A		08-Apr-18		29-Nov-21				0																																																
K10230	Portion VI	0	6d	100%	0	30-Nov-17 A		08-Apr-18		29-Nov-21				0																																																
Subcontracting														404																																																
S10000	Proposal on competitive process for selection of suppliers of Plant and Materials, Equipment and insurance	21	7d	100%	0	20-Nov-17 A	11-Dec-17 A	08-Apr-18	08-Apr-18	27-Jun-19	27-Jun-19	27-Jun-19	591																																																	
S10010	Acceptance of proposal on competitive process	21	7d	100%	0	11-Dec-17 A	18-Dec-17 A	08-Apr-18	08-Apr-18	27-Jun-19	27-Jun-19	27-Jun-19																																																		
S10020	Subcontracting procedure	3	6d	100%	0	04-Dec-17 A	06-Dec-17 A	08-Apr-18	08-Apr-18	09-Apr-18	09-Apr-18	09-Apr-18																																																		
S10030	Acceptance of subcontracting procedure	6	7d	100%	0	07-Dec-17 A	12-Dec-17 A	08-Apr-18	08-Apr-18	09-Apr-18	09-Apr-18	09-Apr-18																																																		
Subcontract Packages														319																																																
S10040	SC003 - Community Liaison Centre subcontract	48	6d	100%	0	07-Dec-17 A	21-Feb-18 A	08-Apr-18	08-Apr-18	09-Apr-18	09-Apr-18	09-Apr-18																																																		
S10050	SC004 - Contractor's site office subcontract	48	6d	100%	0	07-Dec-17 A	08-Feb-18 A	08-Apr-18	08-Apr-18	24-Apr-18	24-Apr-18	24-Apr-18																																																		
S10060	SC002 - Pre-construction condition survey subcontract	48	6d	100%	0	07-Dec-17 A	27-Feb-18 A	08-Apr-18	08-Apr-18	03-May-18	03-May-18	03-May-18																																																		
S10070	SC011 - Instrumentation and ADMS subcontract	48	6d	30%	34	08-Mar-18 A	18-May-18	09-Apr-18	18-May-18	04-May-18	13-Jun-18	21																																																		
S10080	SC005 - Site security system subcontract	48	6d	100%	0	07-Dec-17 A	27-Feb-18 A	08-Apr-18	08-Apr-18	24-May-18	24-May-18	24-May-18																																																		
S10090	SC006 - ICE for temporary works and Contractor's Design works	48	6d	100%	0	07-Dec-17 A	20-Mar-18 A	08-Apr-18	08-Apr-18	09-Apr-18	09-Apr-18	09-Apr-18																																																		
S10100	SC028 - Landscaping subcontract	48	6d	100%	0	07-Dec-17 A	15-Feb-18 A	08-Apr-18	08-Apr-18	09-Apr-18	09-Apr-18	09-Apr-18																																																		
S10110	Traffic consultant (1st stage)	17	6d	100%	0	30-Nov-17 A	08-Dec-17 A	08-Apr-18	08-Apr-18	17-Apr-18	17-Apr-18	17-Apr-18																																																		
S10120	SC008 - Traffic consultant (2nd stage)	48	6d	80%	10	13-Dec-17 A	19-Apr-18	09-Apr-18	19-Apr-18	01-Jun-18	12-Jun-18	44																																																		
S10130	SC013 - Watermain subcontract	48	6d	90%	5	08-Feb-18 A	13-Apr-18	09-Apr-18	13-Apr-18	09-Apr-18	14-Apr-18	0																																																		
S10140	SC014 - Road and drainage subcontract	48	6d	90%	5	22-Jan-18 A	13-Apr-18	09-Apr-18	13-Apr-18	09-Apr-18	14-Apr-18	0																																																		
S10150	SC010 - Ground investigation subcontract	48	6d	30%	34	08-Mar-18 A	18-May-18	09-Apr-18	18-May-18	26-May-18	06-Jul-18	39																																																		
S10160	SC018 - Bored pile subcontract	48	6d	0%	48	02-May-18*	28-Jun-18	02-May-18	28-Jun-18	04-Sep-18	01-Nov-18	104																																																		
S10170	SC019 - Socketted H-pile subcontract	48	6d	0%	48	02-May-18*	28-Jun-18	02-May-18	28-Jun-18	09-Nov-18	07-Jan-19	158																																																		
S10180	SC031 - Road lighting system subcontract	48	6d	0%	48	02-May-18*	28-Jun-18	02-May-18	28-Jun-18	01-Nov-18	28-Dec-18	151																																																		
S10190	SC017 - Fences, railing, parapets, crash gate and untensioned beam barriers	48	6d	0%	48	01-Jun-18*	28-Jul-18	01-Jun-18	28-Jul-18	25-Oct-18	19-Dec-18	120																																																		
S10200	SC015 - Flexible surfacing	48	6d	0%	48	03-Jul-18*	27-Aug-18	03-Jul-18	27-Aug-18	25-Oct-18	19-Dec-18	95																																																		
S10210	SC033 - Electrical system for footbridge subcontract	48	6d	0%	48	03-Jul-18*	27-Aug-18	03-Jul-18	27-Aug-18	12-Jul-19	05-Sep-19	304																																																		
S10220	SC029 - Irrigation system subcontract	48	6d	0%	48	01-Aug-18*	26-Sep-18	01-Aug-18	26-Sep-18	28-Mar-19	29-May-19	196																																																		
S10230	SC030 - Lift system subcontract	48	6d	0%	48	01-Aug-18*	26-Sep-18	01-Aug-18	26-Sep-18	20-Mar-19	21-May-19	189																																																		
S10240	SC022 - Footbridge waterproofing	48	6d	0%	48	01-Sep-18*	30-Oct-18	01-Sep-18	30-Oct-18	28-Mar-20	29-May-20	466																																																		
S10250	SC025 - Glazing subcontract	48	6d	0%	48	02-Oct-18*	27-Nov-18	02-Oct-18	27-Nov-18	05-Jul-19	29-Aug-19	222																																																		
S10260	SC032 - Canopy for footbridge and cladding of arch subcontract	48	6d	0%	48	02-Oct-18*	27-Nov-18	02-Oct-18	27-Nov-18	17-Jun-19	12-Aug-19	207																																																		
S10270	SC020 - Footbridge RC works subcontract	48	6d	0%	48	01-Nov-18*	28-Dec-18	01-Nov-18	28-Dec-18	25-Jan-19	25-Mar-19	70																																																		
S10280	SC021 - Prestressing, bearing and fabricated movement joint subcontract	48	6d	0%	48	01-Nov-18*	28-Dec-18	01-Nov-18	28-Dec-18	25-Jul-19	19-Sep-19	214																																																		
S10290	SC023 - Footbridge steelworks (steel arch & lift beams)	48	6d	0%	48	01-Nov-18*	28-Dec-18	01-Nov-18	28-Dec-18	05-Nov-19	02-Jan-20	299																																																		
S10300	SC026 - Footbridge finishing	48	6d	0%	48	01-Nov-18*	28-Dec-18	01-Nov-18	28-Dec-18	13-Jun-20	10-Aug-20	477																																																		
General Submissions														974																																																
C10000	Draft Safety Plan (submission)	14	7d	100%	0	20-Nov-17 A	20-Jul-20	08-Apr-18	20-Jul-20	09-Apr-18	28-Sep-20	70																																																		
C10010	Safety Plan (submission)	6	6d	100%	0	20-Dec-17 A	06-Jan-18 A	08-Apr-18	08-Apr-18	17-Apr-18	17-Apr-18																																																			
C10020	Safety Plan (PM's acceptance)	21	7d	100%	0	07-Jan-18 A	24-Jan-18 A	08-Apr-18	08-Apr-18	17-Apr-18	17-Apr-18																																																			
C10030	Environmental Management Plan (prepare & submit)	21	7d	100%	0	20-Nov-17 A	11-Dec-17 A	08-Apr-18	08-Apr-18	17-Apr-18	17-Apr-18																																																			
C10040	Environmental Management Plan (review & discuss)	6	7d	100%	0	12-Dec-17 A	11-Jan-18 A	08-Apr-18	08-Apr-18	17-Apr-18	17-Apr-18																																																			

Detailed First Programme (DWP-R0)
 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

NE/2017/02 - Tseung Kwan O - Lam Tin Tunnel
Road P2/D4 and Associated Works
Updated Programme

Date	Revision	Checked	Approved
09-Apr-18	RWP-2018-04 (Data date 8-Apr-18)	TC	

NE/2017/02 - Updated Programme (April 2018)

Activity ID	Activity Name	Original Duration	Calendar	Activity % Complete	Remaining Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Float	Time Risk Allowance	2018												2019												2020												2021											
														Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
Glazing System																																																													
C12200	Design of glazing system (prepare & submit)	90	6d	0%	90	01-Jun-19	28-Nov-20	01-Jun-19	28-Nov-20	30-Aug-19	28-Nov-20	0																																																	
C12210	Design of glazing system (review & discuss)	18	6d	0%	18	18-Sep-19	10-Oct-19	18-Sep-19	10-Oct-19	17-Dec-19	09-Jan-20	75																																																	
C12220	Design of glazing system (resubmit)	18	6d	0%	18	11-Oct-19	31-Oct-19	11-Oct-19	31-Oct-19	10-Jan-20	03-Feb-20	75																																																	
C12230	Design of glazing system (accept)	21	7d	0%	21	01-Nov-19	21-Nov-19	01-Nov-19	21-Nov-19	04-Feb-20	24-Feb-20	95																																																	
C12240	MS for glazing system (prepare & submit)	18	6d	0%	18	22-Nov-19	12-Dec-19	22-Nov-19	12-Dec-19	31-Mar-20	24-Apr-20	105																																																	
C12250	MS for glazing system (review & discuss)	18	6d	0%	18	13-Dec-19	06-Jan-20	13-Dec-19	06-Jan-20	25-Apr-20	18-May-20	105																																																	
C12260	MS for glazing system (resubmit)	12	6d	0%	12	07-Jan-20	20-Jan-20	07-Jan-20	20-Jan-20	19-May-20	01-Jun-20	105																																																	
C12270	MS for glazing system (accept)	21	7d	0%	21	21-Jan-20	10-Feb-20	21-Jan-20	10-Feb-20	02-Jun-20	22-Jun-20	133																																																	
C12280	Material order and delivery of glazing system	96	6d	0%	96	22-Nov-19	19-Mar-20	22-Nov-19	19-Mar-20	25-Feb-20	22-Jun-20	75																																																	
C12290	Install glazing system (lift)	30	6d	0%	30	20-Mar-20	28-Apr-20	20-Mar-20	28-Apr-20	23-Jun-20	29-Jul-20	75																																																	
C12300	Install glazing system (canopy)	100	6d	0%	100	31-Jul-20	28-Nov-20	31-Jul-20	28-Nov-20	01-Aug-20	28-Nov-20	0																																																	
Road Lighting System																																																													
C12310	Design of road lighting system (prepare & submit)	90	6d	0%	90	02-Oct-18	18-Jan-19	02-Oct-18	18-Jan-19	29-Dec-18	18-Apr-19	73																																																	
C12320	Design of road lighting system (review & discuss)	18	6d	0%	18	19-Jan-19	12-Feb-19	19-Jan-19	12-Feb-19	23-Apr-19	15-May-19	73																																																	
C12330	Design of road lighting system (resubmit)	18	6d	0%	18	13-Feb-19	05-Mar-19	13-Feb-19	05-Mar-19	16-May-19	05-Jun-19	73																																																	
C12340	Design of road lighting system (accept)	21	7d	0%	21	06-Mar-19	26-Mar-19	06-Mar-19	26-Mar-19	06-Jun-19	26-Jun-19	92																																																	
C12350	MS for road lighting system (prepare & submit)	18	6d	0%	18	27-Mar-19	17-Apr-19	27-Mar-19	17-Apr-19	05-Aug-19	24-Aug-19	104																																																	
C12360	MS for road lighting system (review & discuss)	18	6d	0%	18	18-Apr-19	14-May-19	18-Apr-19	14-May-19	26-Aug-19	16-Sep-19	104																																																	
C12370	MS for road lighting system (resubmit)	12	6d	0%	12	15-May-19	28-May-19	15-May-19	28-May-19	17-Sep-19	30-Sep-19	104																																																	
C12380	MS for road lighting system (accept)	21	7d	0%	21	29-May-19	18-Jun-19	29-May-19	18-Jun-19	01-Oct-19	21-Oct-19	125																																																	
C12390	Material order and delivery of road lighting system	96	6d	0%	96	27-Mar-19	25-Jul-19	27-Mar-19	25-Jul-19	27-Jun-19	21-Oct-19	72																																																	
C12400	Install road lighting system	144	6d	0%	144	19-Oct-19	16-Apr-20	19-Oct-19	16-Apr-20	22-Oct-19	17-Apr-20	1																																																	
C12410	Testing and commissioning of road lighting system	24	6d	0%	24	16-Apr-20	16-May-20	16-Apr-20	16-May-20	18-Apr-20	18-May-20	1																																																	
Stage 0 Works																																																													
Preliminary Works																																																													
C12420	Application of XP	75	6d	100%	0	01-Dec-17 A	05-Mar-18 A	08-Apr-18	08-Apr-18	17-Apr-18	17-Apr-18	14																																																	
C12430	Utilities detection (Road P2 south of interchange)	6	6d	100%	0	13-Jan-18 A	18-Jan-18 A	08-Apr-18	08-Apr-18	23-May-18	23-May-18																																																		
C12440	Initial site survey	6	6d	100%	0	11-Dec-17 A	30-Dec-17 A	08-Apr-18	08-Apr-18	17-Apr-18	17-Apr-18																																																		
C12450	Pre-construction condition survey and manhole survey	24	6d	100%	0	08-Mar-18 A	23-Mar-18 A	08-Apr-18	08-Apr-18	03-May-18	03-May-18																																																		
C12460	Contractor's site office	30	6d	75%	8	10-Jan-18 A	16-May-18*	07-May-18	16-May-18	24-May-18	01-Jun-18	14																																																	
Stage 1 Works																																																													
TTA Stage 1A																																																													
TTA																																																													
C12470	Design and acceptance of TTA Stage 1A, 1B-1 and 1B-2	42	6d	100%	0	20-Dec-17 A	20-Feb-18 A	08-Apr-18	08-Apr-18	17-Apr-18	17-Apr-18	0																																																	
C12480	Implementation of TTA Stage 1A (trial pits)	2	6d	100%	0	08-Mar-18 A	09-Mar-18 A	10-Apr-18	10-Apr-18	17-Apr-18	17-Apr-18	1																																																	
C12490	Implementation of TTA Stage 1A (roundabout)	2	6d	50%	1	19-Mar-18 A	11-Apr-18	10-Apr-18	11-Apr-18	17-Apr-18	17-Apr-18	6																																																	
C12500	Utilities detection (Po Shun Road north of interchange)	4	6d	100%	0	13-Jan-18 A	18-Jan-18 A	11-Apr-18	11-Apr-18	18-Apr-18	18-Apr-18																																																		
C12510	Modification of road layout at roundabout	12	6d	0%	12	16-Apr-18	30-Apr-18	16-Apr-18	30-Apr-18	18-Apr-18	02-May-18	1																																																	
C12520	Temporary footpath and cycle track at south of Chui Ling Road / Po Yap Road (for TTA Stage 1B-1 and 1B-2)	12	6d	0%	12	16-Apr-18	30-Apr-18	16-Apr-18	30-Apr-18	18-Apr-18	02-May-18	1																																																	
C12530	Tree felling (Road P2 south of interchange)	12	6d	100%	0	08-Feb-18 A	12-Feb-18 A	11-Apr-18	11-Apr-18	29-May-18	29-May-18																																																		
C12540	Tree transplanting (Road P2 south of interchange)	48	6d	0%	48	16-Apr-18	13-Jun-18	16-Apr-18	13-Jun-18	17-Apr-18	13-Jun-18	0																																																	
TTA Stage 1B-1 & 1B-2																																																													
TTA																																																													
C12550	Implementation of TTA Stage 1B-1	2	6d	0%	2	30-Apr-18	03-May-18	30-Apr-18	03-May-18	03-May-18	04-May-18	1	1																																																
C12560	Implementation of TTA Stage 1B-2	2	6d	0%	2	18-May-18	21-May-18	18-May-18	21-May-18	06-Jul-18	07-Jul-18	38	1																																																
C12570	Utilities detection (Chui Ling Road south - existing cycle track)	6	6d	0%	6	03-May-18	10-May-18	03-May-18	10-May-18	07-Sep-18	13-Sep-18	105																																																	
C12580	Tree felling (Po Yap Road)	12	6d	0%	12	03-May-18	17-May-18	03-May-18	17-May-18	12-Oct-18	26-Oct-18	133																																																	
C12590	Tree transplanting (Po Yap Road)	54	6d	0%	54	07-May-18	12-Jul-18	07-May-18	12-Jul-18	27-Sep-18	30-Nov-18	118																																																	
C12600	Modification of central median (Po Yap Road)	36	6d	0%	36	05-Jun-18	19-Jul-18	05-Jun-18	19-Jul-18	27-Oct-18	07-Dec-18	118																																																	
C12610	Tree transplanting (adjacent TKO Sports Centre)	48	6d	0%	48	03-May-18	30-Jun-18	03-May-18	30-Jun-18	05-May-18	03-Jul-18	71																																																	
C12620	Temporary footpath and cycle track (for TTA Stage 1C)	18	6d	0%	18	03-May-18	25-May-18	03-May-18	25-May-18	30-Jul-18	18-Aug-18	71																																																	
C12630	Tree transplanting (Chui Ling Road)	48	6d	0%	48	07-May-18	05-Jul-18	07-May-18	05-Jul-18	26-Jul-18	19-Sep-18	65																																																	
C12640	Install instrumentation and ADMS	18	6d	0%	18	23-Jul-18	13-Aug-18	23-Jul-18	13-Aug-18	18-Aug-18	07-Sep-18	22																																																	
C12650	Modification of central median (Chui Ling Road)	36	6d	0%	36	21-May-18	05-Jul-18	21-May-18	05-Jul-18	09-Jul-18	18-Aug-18	38																																																	
Drainage																																																													
C12660	Stormwater SMH5101-SMH5102 and SMH5102-SMH9201	19	6d	0%	19	28-May-18	20-Jun-18	28-May-18	20-Jun-18	29-May-18	20-Jun-18	0	1																																																
C12670	Stormwater 900 dia. near Pier 02 and connection to manholes	42	6d	0%	42	30-Jun-18	20-Aug-18	30-Jun-18	20-Aug-18	04-Jul-18	21-Aug-18	1	1																																																
C12680	Stormwater SMH6602-SMH5001, SMH5001-SMH5002, SMH5002-SMH9501	24	6d	0%	24	21-May-18	20-Jun-18	21-May-18	20-Jun-18	23-May-18	20-Jun-18	0	1																																																
Utilities																																																													
C12690	Gas main at Chui Ling Road (South) by HKCG	19	6d	0%	19	03-May-18	24-Jul-18	03-May-18	24-Jul-18	28-Jul-18	18-Aug-18	70	1																																																
C12700	Gas main at Po Shun Road by HKCG	19	6d	0%	19	30-Jun-18	24-Jul-18	30-Jun-18	24-Jul-18	28-Jul-18	18-Aug-18	22	1																																																
Fresh Watermain																																																													
C12830	Fresh watermain CHB 0 to 37.202, CHC 0 to 74.858, CHD 0 to 29.591	53	6d	0%	53	20-Jun-18	22-Aug-18	20-Jun-18	22-Aug-18	21-Jun-18	22-Aug-18	0																																																	
TTA Stage 1C																																																													
TTA																																																													
C12740	Design and acceptance of TTA Stage 1C	42	6d	0%	42	19-Apr-18	23-Aug-18	19-Apr-18	23-Aug-18	13-Jun-18	30-Oct-18	55																																																	
C12750	Implementation of TTA Stage 1C	2	6d	0%	2	24-Jul-18	26-Jul-18	24-Jul-18	26-Jul-18	20-Aug-18	21-Aug-18	22	1																																																
C12760	Temporary footpath and cycle track (for TTA Stage 1D)	24	6d	0%	24	26-Jul-18	23-Aug-18	26-Jul-18	23-Aug-18	02-Oct-18	30-Oct-18	55																																																	
C12770	Tree felling (Chui Ling Road)	12	6d	0%	12	26-Jul-18	09-Aug-18	26-Jul-18	09-Aug-18	22-Aug-18	04-Sep-18	22																																																	
Utilities																																																													
C12780	Telecom cables at Chui Ling Road by HGC, CATV, PCCW (incl. Chui Shin Street)	19	6d	0%	19	09-Aug-18	31-Aug-18	09-Aug-18	31-Aug-18	05-Sep-18	27-Sep-18	22	1																																																
C12790	11kV cables at Po Shun Road by CLPP	19	6d	0%	19	20-Aug-18	11-Sep-18	20-Aug-18	11-Sep-18	22-Aug-18	12-Sep-18	1	1																																																
C12800	Gas main at Chui Ling Road (North and central median) by HKCG	19	6d	0%	19	11-Sep-18	05-Oct-18	11-Sep-18	05-Oct-18	13-Sep-18	06-Oct-18	1	1																																																

Detailed First Programme (DWP-R0) Actual Work
 Remaining Work Critical Remaining Work
 Milestone Summary

NE/2017/02 - Tseung Kwan O - Lam Tin Tunnel
 Road P2/D4 and Associated Works
 Updated Programme

Date	Revision	Checked	Approved
09-Apr-18	RWP-2018-04 (Data date 8-Apr-18)	TC	

Subject: 3 Months Look Ahead Programme			
Activities	May,18	Jun,18	Jul,18
Erection of falsework system			
Construction of Pile Cap PC4 and Sump Pit			
Install steel mould for main deck			

Subject: Construction Programme (Apr, 2018)				
Activities	Week 1	Week 2	Week 3	Week 4
Erection of falsework system				

Activity ID	Activity Name	Original Duration	Start	Finish	2018			
					Apr	May	Jun	Jul
Tseung Kwan O Lam Tin Tunnel - Tseung Kwan O Interchange and Associated Works _180316 1709								
Construction Works								
Construction Works of Contractor Site Accommodation								
CON-10010	Erect hoarding and construct contractor's site accommodation (CSA)	18	03-Apr-18	24-Apr-18				
CON-10020	Maintenance CSA during contract period	862	25-Apr-18	19-Mar-21				
Temporary Platform and Ground Investigation								
Ground Investigation Works (Including Erection Temporary Work)								
Phase I - Portion I & V								
CON-10070	Ground Investigation works (Phase 1) (1no SI/Team/8days),Including Temporary Work, Plant Mobilization, Testing - 4 rigs	102	16-May-18	14-Sep-18				
Bored Pile Construction & Pile Test (59nos)(Including Removal of Temporary Work)								
Bored Pile Construction at Bridge ML								
CON-10100	Bored Pile, Pile Test & Removal of Temporary Work for ML 1G, 2 Piles (1pile/1.5mon, team 1)	108	07-Jul-18	13-Nov-18				
CON-10110	Bored Pile, Pile Test & Removal of Temporary Work for ML 1F-N, 2 Piles (1pile/1.5mon, team 2)	108	07-Jul-18	13-Nov-18				
CON-10120	Bored Pile, Pile Test & Removal of Temporary Work for ML 1F-S, 2 Piles (1pile/1.5mon, team 3)	108	07-Jul-18	13-Nov-18				
Bored Pile Construction at Bridge S300								
CON-10180	Bored Pile, Pile Test & Removal of Temporary Work for S300 4A, 1 Pile (1pile/1.5mon, team 4)	69	07-Jul-18	26-Sep-18				

- Potential Compensation Events
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ ◆ Milestone

NE/2017/01 Tseung Kwan O - Lam Tin Tunnel
Tseung Kwan O Interchange and Associated Works

Construction Programme (Period: 1-4-2018 to 31-7-2018)


NE/2017/01

**APPENDIX R
RECORD OF LANDFILL GAS
MONITORING BY CONTRACTOR**


APPENDIX R - RECORD OF LANDFILL GAS MONITORING BY THE CONTRACTOR

Location	Date of Measurement	Sampling time	Weather Condition	Temperature (°C)	Methane (%)	Carbon dioxide (%)	Oxygen (%)
Portion III	3-Apr-18	08:30	Sunny	25	0	0	20.9
	3-Apr-18	13:01	Sunny	29	0	0	20.9
	4-Apr-18	08:30	Sunny	24	0	0	20.9
	4-Apr-18	13:02	Sunny	28	0	0	20.9
	6-Apr-18	08:30	Cloudy	22	0	0	20.9
	6-Apr-18	13:00	Rainy	26	0	0	20.9
	7-Apr-18	08:30	Cloudy	18	0	0	20.9
	7-Apr-18	13:02	Rainy	21	0	0	20.9
	9-Apr-18	08:30	Sunny	18	0	0	20.9
	9-Apr-18	13:01	Sunny	26	0	0	20.9
	10-Apr-18	08:30	Cloudy	21	0	0	20.9
	10-Apr-18	13:00	Cloudy	28	0	0	20.9
	11-Apr-18	08:30	Cloudy	22	0	0	20.9
	11-Apr-18	13:00	Cloudy	27	0	0	20.9
	12-Apr-18	08:30	Sunny	23	0	0	20.9
	12-Apr-18	13:02	Sunny	28	0	0	20.9
	13-Apr-18	08:30	Cloudy	24	0	0	20.9
	13-Apr-18	13:02	Cloudy	30	0	0	20.9
	14-Apr-18	08:30	Cloudy	25	0	0	20.9
	14-Apr-18	13:00	Rainy	30	0	0	20.9
	16-Apr-18	08:30	Cloudy	17	0	0	20.9
	16-Apr-18	13:00	Cloudy	19	0	0	20.9
	17-Apr-18	08:30	Cloudy	17	0	0	20.9
	17-Apr-18	13:00	Cloudy	23	0	0	20.9
	18-Apr-18	08:30	Cloudy	21	0	0	20.9
	18-Apr-18	13:00	Cloudy	26	0	0	20.9
	19-Apr-18	08:30	Cloudy	21	0	0	20.9
	19-Apr-18	13:02	Sunny	16	0	0	20.9
	20-Apr-18	08:30	Rainy	22	0	0	20.9
	20-Apr-18	13:02	Cloudy	26	0	0	20.9
21-Apr-18	08:30	Rainy	23	0	0	20.9	
21-Apr-18	13:00	Cloudy	28	0	0	20.9	
23-Apr-18	08:30	Rainy	24	0	0	20.9	
23-Apr-18	13:01	Rainy	30	0	0	20.9	
24-Apr-18	08:30	Cloudy	23	0	0	20.9	
24-Apr-18	13:00	Cloudy	27	0	0	20.9	
25-Apr-18	08:30	Cloudy	23	0	0	20.9	
25-Apr-18	13:00	Cloudy	25	0	0	20.9	
26-Apr-18	08:30	Cloudy	22	0	0	20.9	
26-Apr-18	13:01	Cloudy	25	0	0	20.9	
27-Apr-18	08:30	Rainy	22	0	0	20.9	
27-Apr-18	13:02	Cloudy	28	0	0	20.9	
28-Apr-18	08:30	Sunny	23	0	0	20.9	
28-Apr-18	13:01	Cloudy	26	0	0	20.9	
30-Apr-18	08:30	Rainy	24	0	0	20.9	
30-Apr-18	13:04	Rainy	29	0	0	20.9	


Methane

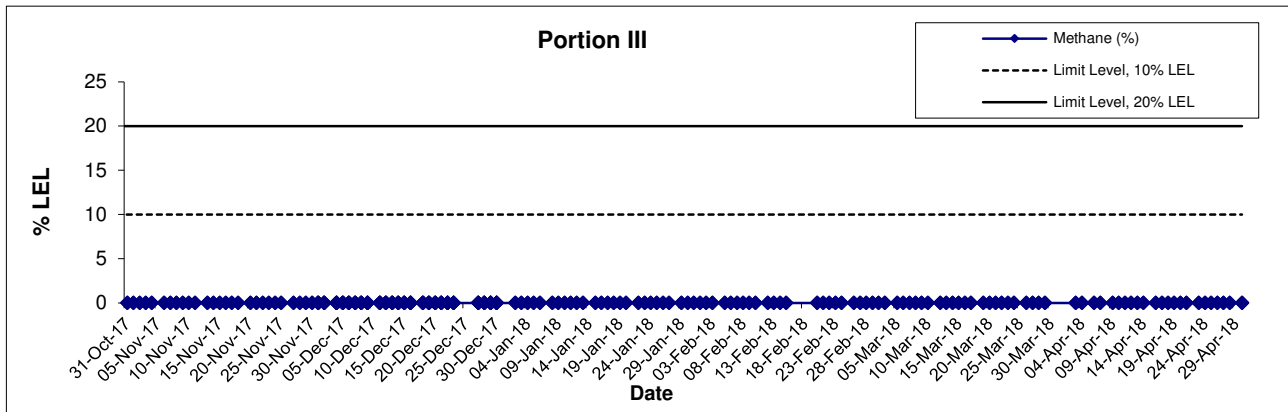

Carbon Dioxide

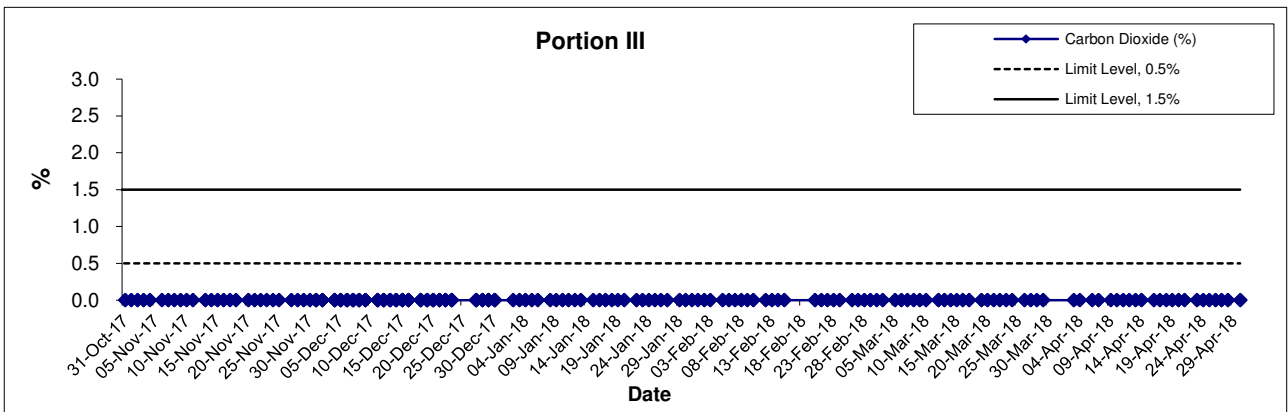

Oxygen

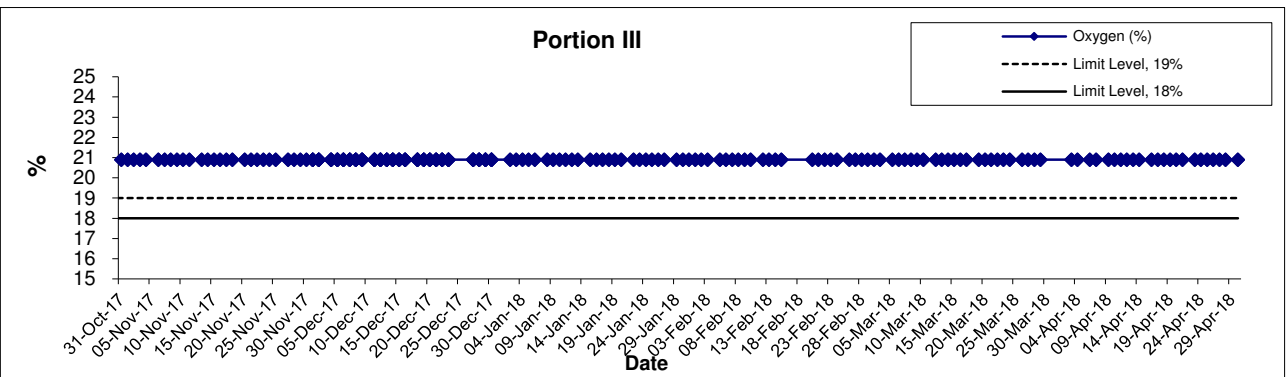

Title	Agreement No. CE 59/2015 (EP)	Scale	Project	CINOTECH
	Environmental Team for Tseung Kwan O - Lam Tin Tunnel – Design and Construction	N.T.S	No. MA16034	
Graphical Presentation of Landfill Gas Measurement	Date	Apr 18	Appendix R	

**APPENDIX S
UPDATED CONSTRUCTION NOISE
ASSESSMENT**

No update on Construction Noise Assessment in the reporting month

**APPENDIX T
CULTURAL HERITAGE MONITORING
RESULTS**

Appendix T – Cultural Heritage Monitoring Results

Date	Time	Tilting			Settlement (mm)			Vibration (mm/s)		
		Angle (deg) between THT-BSP-1 & THT-BSP-2	Angle (deg) between THT-BSP-1 & THT-BSP-3	Angle (deg) between THT-BSP-2 & THT-BSP-3	THT-BSP-1	THT-BSP-2	THT-BSP-3	Measurement Direction		
								Tran	Vertical	Longitudinal
3-Apr-18	13:23	1 : 6896	1 : 14018	-1 : 16901	+3	+1	+2	0.127	0.254	0.254
4-Apr-18	17:13	1 : 6896	1 : 7009	0	+4	+2	+2	0.127	0.254	0.254
6-Apr-18	16:05	1 : 3448	1 : 4673	-1 : 16901	+4	+0	+1	0.127	0.127	0.254
7-Apr-18	10:47	1 : 4597	1 : 7009	-1 : 16901	+4	+1	+2	0.254	0.254	0.127
9-Apr-18	17:03	1 : 4597	1 : 4673	0	+4	+1	+1	0.254	0.254	0.127
10-Apr-18	16:51	1 : 6896	1 : 4673	1 : 16901	+2	+0	-1	0.127	0.254	0.254
11-Apr-18	13:47	0	1 : 14018	1 : 16901	+2	+2	+1	0.254	0.254	0.127
12-Apr-18	11:01	1 : 3448	1 : 4673	-1 : 16901	+4	+0	+1	0.254	0.254	0.127
13-Apr-18	9:14	1 : 6896	1 : 7009	0	+3	+1	+1	0.254	0.254	0.127
14-Apr-18	14:30	1 : 4597	1 : 7009	-1 : 16901	+4	+1	+2	0.254	0.254	0.127
16-Apr-18	17:05	1 : 6896	1 : 7009	0	+3	+1	+1	0.254	0.254	0.127
17-Apr-18	17:12	1 : 6896	1 : 14018	-1 : 16901	+3	+1	+2	0.254	0.254	0.127
18-Apr-18	13:37	1 : 4597	1 : 7009	-1 : 16901	+3	+0	+1	0.254	0.254	0.127
19-Apr-18	16:55	1 : 4597	1 : 7009	-1 : 16901	+2	-1	+0	0.254	0.254	0.127
20-Apr-18	16:52	1 : 4597	1 : 7009	-1 : 16901	+3	+0	+1	0.254	0.254	0.127
21-Apr-18	15:52	1 : 4597	1 : 7009	-1 : 16901	+3	+0	+1	0.254	0.254	0.127
23-Apr-18	17:10	-1 : 13792	-1 : 14018	0	+2	+3	+3	0.254	0.254	0.127
24-Apr-18	17:20	1 : 6896	1 : 7009	0	+4	+2	+2	0.254	0.254	0.127
25-Apr-18	17:11	1 : 13792	1 : 14018	0	+3	+2	+2	0.254	0.254	0.127
26-Apr-18	17:02	1 : 13792	1 : 4673	1 : 8451	+2	+1	-1	0.127	0.127	0.254
27-Apr-18	15:34	1 : 3448	1 : 4673	-1 : 16901	+4	+0	+1	0.127	0.127	0.254
28-Apr-18	10:26	0	1 : 14018	1 : 16901	+2	+2	+1	0.254	0.254	0.127
30-Apr-18	16:20	1 : 4597	1 : 7009	-1 : 16901	+3	+0	+1	0.254	0.254	0.127
Alert Level			1:2000			6			4.5	
Alarm Level			1:1500			8			4.8	
Action Level			1:1000			10			5	

Note: **Bold** means Alert Level exceedance**Bold Italic** means Alarm Level exceedance**Bold Italic with underline** means Action Level exceedance
