Leighton-China States Joint Venture

# Contract SCL1123 – Exhibition Station & Western Approach Tunnel

Monthly EM&A Report No. 11

for

FEP-13/364/2009/H & FEP-03/376/2009

[Period from 1 to 30 November 2021]

(December 2021)

Verified by: Claudine LEE

Position: Independent Environmental Checker

Date: 14 December 2021

Leighton-China State Joint Venture

# Contract SCL1123 – Exhibition Station & Western Approach Tunnel

Monthly EM&A Report No.11

for

## FEP-13/364/2009/H & FEP-03/376/2009

[Period from 1 to 30 November 2021]

(December 2021)

Verified by:	FUNG Yiu Wah	h	/
		/	

Position: Environmental Team Leader

Date: 13 December 2021



Leighton – China State J.V.

## Shatin to Central Link -Hung Hom to Admiralty Section

## Works Contract 1123 -CEDD Entrusted Work for Road P2 & other roads and Slip Road 3

## Monthly EM&A Report for November 2021

[December 2021]

	Name	Signature
Prepared & Checked:	Barry Ho	Ao
Reviewed, Approved & Certified:	Y W Fung (Contractor's Environmental Team Leader)	11/

Version: 0

Date: 13 November 2021

#### Disclaimer

This Environmental Monitoring and Audit Report is prepared for Leighton – China State J.V. and is given for its sole benefit in relation to and pursuant to SCL1123 and may not be disclosed to, quoted to or relied upon by any person other than Leighton – China State J.V. without our prior written consent. No person (other than Leighton – China State J.V. into whose possession a copy of this report comes may rely on this plan without our express written consent and Leighton – China State J.V. may not rely on it for any purpose other than as described above.

AECOM Asia Co. Ltd. 12/F, Grand Central Plaza, Tower 2, 138 Shatin Rural Committee Road, Shatin, NT, Hong Kong Tel: (852) 3922 9000 Fax: (852) 2317 7609 www.aecom.com

## **Table of Contents**

Page

EXECU	ITIVE SUMMARY1
1	INTRODUCTION
1.1 1.2	Purpose of the Report3 Report Structure
2	PROJECT INFORMATION
2.1 2.2 2.3 2.4 2.5	Background       4         Site Description       4         Construction Programme and Activities       5         Project Organisation       6         Status of Environmental Licences, Notification and Permits       7
3	ENVIRONMENTAL MONITORING REQUIREMENT8
3.1 3.2	Construction Dust Monitoring
4	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES
5	MONITORING RESULTS
5.1 5.2 5.3	Construction Dust Monitoring
6	ENVIRONMENTAL SITE INSPECTION AND AUDIT16
7	ENVIRONMENTAL NON-CONFORMANCE17
7.1 7.2 7.3 7.4	Summary of Monitoring Exceedances       17         Summary of Environmental Non-Compliance       17         Summary of Environmental Complaints       17         Summary of Environmental Summon and Successful Prosecutions       17
8	FUTURE KEY ISSUES
8.1 8.2 8.3	Construction Programme for the Next Three Month
9	CONCLUSIONS AND RECOMMENDATIONS
9.1 9.2	Conclusions

i

## List of Tables

Table 2.1	Contact	Information	ofKo	
	Contact	Information	or ney	/ Personner

- Table 2.2
   Status of Environmental Licenses, Notifications and Permits
- Table 3.1Air Quality Monitoring Equipment
- Table 3.2 Locations of Construction Dust Monitoring Station
- Table 3.3
   Noise Monitoring Parameters, Frequency and Duration
- Table 3.4
   Noise Monitoring Equipment for Regular Noise Monitoring
- Table 3.5
   Noise Monitoring Station during Construction Phase
- Table 4.1
   Status of Required Submission under Further Environmental Permit
- Table 5.1
   Summary of 24-hour TSP Monitoring Result in the Reporting Period
- Table 5.2
   Summary of 1-hour TSP Monitoring Result in the Reporting Period
- Table 5.3
   Summary of Construction Noise Monitoring Results in the Reporting Period
- Table 6.1
   Observations and Recommendations of Site Audit

## **List of Figures**

Figure 1.1	Site Layout Plan of CEDD Entrusted Works under Contract 1123
Figure 3.1	Air Quality and Noise Monitoring Locations for CEDD Entrusted Works

## List of Appendices

- Appendix A Construction Programme
- Appendix B Project Organisation Structure
- Appendix C Implementation Schedule of Environmental Mitigation Measures
- Appendix D Summary of Action and Limit Levels
- Appendix E Calibration Certificates of Equipment
- Appendix F EM&A Monitoring Schedules
- Appendix G Air Quality Monitoring Results and their Graphical Presentations
- Appendix H Noise Monitoring Results and their Graphical Presentations
- Appendix I Event and Action Plan
- Appendix J Cumulative Statistics on Complaints, Notification of Summons and Successful Prosecutions
- Appendix K Monthly Summary Waste Flow Table

## EXECUTIVE SUMMARY

Shatin to Central Link Contract 1123 – CEDD Entrusted Work for Road P2 & other roads and Slip Road 3 (hereafter called "the Project") covers part of the construction of CEDD entrusted work under the granted Further Environmental Permit: FEP–03/376/2009 and FEP–13/364/2009 respectively.

The Project comprises the construction of Road P2 and other roads which are classified as primary/district distributor roads and Slip Road 3.

The EM&A programme commenced on 25 January 2021. The impact EM&A for the Project includes air quality and noise monitoring.

This report documents the findings of EM&A works conducted in the period between 1 and 30 November 2021. As informed by the Contractor, major activities in the reporting period were:

Location	Site Activities
Road P2 – West (Slip Road 3)	<ul> <li>Drainage and Road works</li> <li>TTM 3 was implemented on 27 November 2021.</li> </ul>
Road P2 – East (Hung Hing Road)	<ul><li>Drainage works</li><li>Road pavement</li></ul>
Road P2 – Permanent PTI (Public Transport Interchange)	<ul> <li>Drainage works</li> <li>Road works (concrete pavement and asphalt)</li> </ul>

## Breaches of Action and Limit Levels for Air Quality

No exceedance of Action and Limit Level of air quality was recorded in the reporting month.

#### Breaches of Action and Limit Levels for Noise

#### Regular Noise Monitoring

No Action Level exceedance was recorded since no noise related complaint was received in the reporting month.

No exceedance of Limit Level of noise was recorded in the reporting month.

## Complaint, Notification of Summons and Successful Prosecution

No complaint, notification of summons and successful prosecution were received in the reporting month.

## **Reporting Changes**

There was no reporting change in the reporting month.

## **Future Key Issues**

Key issues to be considered in the next three months included:

Location	Site Activities
Road P2 –	Underground Drainage
West (Slip Road 3)	Road works
Road P2 –	Drainage works
East (Hung Hing Road)	Underground Utilities
	Road works (TTM)
Road P2 – PTI	Drainage & UU works
(Public Transport	Road works (TTM)
Interchange)	Footpath pavement
	Relocation of temporary PTI

Potential environmental impacts arising from the above construction activities are mainly associated with construction dust, construction noise, water quality and waste management.

## 1 INTRODUCTION

Leighton – China State Joint Venture (JV) was commissioned by MTR as the Civil Contractor for CEDD Entrusted Works under Contract 1123. AECOM Asia Company Limited (AECOM) was appointed by JV as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme during construction phase of the Project.

## 1.1 Purpose of the Report

1.1.1 This is the eleven monthly EM&A Report which summaries the impact monitoring results and audit findings for the Project during the reporting period between 1 and 30 November 2021.

## 1.2 Report Structure

- 1.2.1 This monthly EM&A Report is organized as follows:
  - Section 1: Introduction
  - Section 2: Project Information
  - Section 3: Environmental Monitoring Requirement
  - Section 4: Implementation Status of Environmental Mitigation Measures
  - Section 5: Monitoring Results
  - Section 6: Environmental Site Inspection and Audit
  - Section 7: Environmental Non-conformance
  - Section 8: Future Key Issues
  - Section 9: Conclusions and Recommendations

## 2 **PROJECT INFORMATION**

## 2.1 Background

- 2.1.1 Road P2 and other roads which are classified as primary/district distributor roads identified as DP2 which covered in the Environmental Permit No. EP-376/2009 in the approved Wan Chai Development Phase II (WDII) and Central Wan Chai Bypass (CWB) comprising (i) a dual 2-lane primary distributor road, Road P2; and (ii) other new primary and district distributor roads connecting to the slip roads of the Central-Wan Chai Bypass.
- 2.1.2 Slip road 3 identified as part of DP1 which covered in the Environmental Permit No. EP-364/2009/H in the approved Wan Chai Development Phase II (WDII) and Central Wan Chai Bypass (CWB) comprising (i) slip roads to connect the CWB to the local road system in the Wan Chai North and Causeway Bay area; and (ii) associated road lighting, road signing, traffic control and surveillance system (iii) other associated works.
- 2.1.3 The Environmental Impact Assessment Report for Central - Wan Chai Bypass and Island Eastern Corridor Link (CWB&IECL) EIA Report (Register No. AEIAR-041/2001) and the Wan Chai Development Phase II and Central-Wan Chai Bypass (WDII&CWB) EIA Report (Register No. AEIAR-125/2008) which were approved on 31 August 2001 and 11 December 2008 under the Environmental Impact Assessment Ordinance (EIAO). Following the approval of the EIA Report, an Environmental Permits (EPs) were granted on 13 November 2009 and 22 April 2020 respectively, which covers Road P2 and other roads which are classified as primary/district distributor roads [DP2] and Central – Wan Chai Bypass (CWB) including its Road Tunnel and Slip Roads [DP1] (EP No.: EP-376/2009 and EP-364/2009/H), for the construction and operation. Further Environmental Permits (FEP No. FEP-03/376/2009 and FEP-13/364/2009/H) were both subsequently granted from the Director of Environmental Protection (DEP) on 2 June 2020, which cover the construction works for DP2 and a part of DP1 respectively.
- 2.1.4 The site layout plan of the Project is shown in **Figure 1.1**.

## 2.2 Site Description

- 2.2.1 The major construction activities under CEDD Entrusted Works of Contract 1123 include:
  - (a) Site preparation;
  - (b) Construct for dual 2-lane primary distributor road, Road P2;
  - (c) Construct for other new primary and district distributor roads connecting to the slip roads of the Central-Wan Chai Bypass;
  - (d) Construct for slip roads to connect the CWB to the local road system in the Wan Chai North and Causeway Bay area;
  - (e) Construct for associated road lighting, road signing, traffic control and surveillance system; and
  - (f) Construct for other associated works;

## 2.3 Construction Programme and Activities

2.3.1	The major construction activities undertaken in the reporting month are summarised below:

Location	Site Activities		
Road P2 – West (Slip Road 3)	<ul><li>Drainage and Road works</li><li>TTM 3 was implemented on 27 November 2021.</li></ul>		
Road P2 – East (Hung Hing Road)	<ul><li>Drainage works</li><li>Road pavement</li></ul>		
Road P2 – Permanent PTI (Public Transport Interchange)	<ul> <li>Drainage works</li> <li>Road works (concrete pavement and asphalt)</li> </ul>		

2.3.2 The construction programme is presented in **Appendix A**.

## 2.4 **Project Organisation**

2.4.1 The project organization structure is shown in **Appendix B**. The key personnel contact names and numbers for the Project are summarised in **Table 2.1**.

Table 2.1	<b>Contact Information</b>	of Kev Personnel
	••••••••••••••••••••••••••••••••••••••	

Party	Role	Position	Name	Telephone	Fax
MTR	Residential	Senior Construction Manager – SCL Civil	Mr. Mike Bezzano	3959 2128	3959 2200
	Engineer (ER)	SCL Project Environmental Team Leader	Ms. Lisa Poon	3127 6295	3127 6422
Meinhardt	Independent Environmental Checker	Independent Environmental Checker	Ms. Claudine Lee	2859 5409	2540 1580
JV	Contractor	Project Director	Mr. Brian Shepstone	3973 0838	31051126
5V Contractor		Environmental Engineer	Mr. Andy Leung	3973 1498	31031120
AECOM	Contractor's Environmental Team (ET)	ET Leader	Mr. Y W Fung	3922 9366	2317 7609

## 2.5 Status of Environmental Licences, Notification and Permits

2.5.1 Relevant environmental licenses, permits and/or notifications on environmental protection for this Project and valid in the reporting month are summarized in **Table 2.2**.

 Table 2.2
 Status of Environmental Licenses, Notifications and Permits

Permit / License No.	Valid I	Period		Remarks		
/ Notification/ Reference No.	From	То	Status			
Environmental Permit						
FEP-03/376/2009	2 Jun 2020	End of Contract	Valid			
FEP-13/364/2009/H	2 Jun 2020	End of Contract	Valid			
Construction Noise Pe	ermit					
-	-	-	-	-		
Wastewater Discharge	e License¹					
-	-	-	-	-		
Chemical Waste Prod	ucer Registratio	n				
5213-135-L2881-01	02 Apr 2015	End of Contract	Valid	For whole site at Wan Chai Area		
Marine Dumping Perm	nit					
-	-	-	-	-		
Billing Account for Co	Billing Account for Construction Waste Disposal					
7021736	16 Feb 2015	End of Contract	Valid	For Disposal of C&D Waste		
Notification Under Air Pollution Control (Construction Dust) Regulation						
385128 Bomarki	1 Mar 2015	End of Contract	Valid	For whole site at Wan Chai Area		

Remark:

1. The Contractor was reminded to keep tracking on the site conditions and review its application for wastewater discharge license.

## 3 ENVIRONMENTAL MONITORING REQUIREMENT

## 3.1 Construction Dust Monitoring

## Monitoring Requirements

3.1.1 In accordance with the approved EM&A Manuals, 24-hour and 1-hour Total Suspended Particulates (TSP) levels at the designated air quality monitoring station is required. Impact 24-hour monitoring should be carried out for at least once every 6 days and 1-hour TSP monitoring should be done at least 3 times every 6 days while the highest dust impact is expected. The Action and Limit level of the air quality monitoring is provided in **Appendix D**.

## Monitoring Equipment

- 3.1.2 24-hour TSP air quality monitoring was performed using High Volume Sampler (HVS) located at the designated monitoring stations. The HVS meets all the requirements of the EM&A Manual.
- 3.1.3 A portable direct reading dust meter was used to carry out the 1-hour TSP monitoring.
- 3.1.4 Brand and model of the equipment is given in **Table 3.1**.

## Table 3.1 Air Quality Monitoring Equipment

Equipment Brand and Model	
High Volume Sampler (24-hour TSP)	Andersen Total Suspended Particulate Mass Flow Controlled High Volume Air Sampler (Model No. GS 2310 (S/N:10273)) (Model No. GS 2310 (S/N:3384))
Calibration Kit (24-hour TSP)	TISCH Environmental Orifice (Model TE-5025A (S/N: 843))
Portable direct reading dust meter (1-hour TSP)	Sibata Digital Dust Monitor (Model No. LD-3)

#### Monitoring Locations

3.1.5 The monitoring station for construction dust monitoring pertinent to the Project has been identified based on the approved EM&A Manual for SCL (HUH-ADM) of the Project. The location of the construction dust monitoring stations are summarised in **Table 3.2** and shown in **Figure 3.1**.

Table 3.2	Locations of Construction Dust Monitoring Station
-----------	---

Station ID	Dust Monitoring Station
CMA5b <sup>1</sup>	Pedestrian Plaza
CMA6a <sup>1</sup>	WDII PRE Site Office

Remark:

1. According to the updated site layout of CEDD Entrusted Works and Updated EM&A Manual for EP-376/2009 and EP-364/2009, Pedestrian Plaza (CMA5b) and WDII PRE Site Office (CMA6A) were selected as the most affected sensitive receiver during the construction phase.

#### Monitoring Methodology

- 3.1.6 24-hour TSP Monitoring
  - (a) The HVS was installed in the vicinity of the air sensitive receivers. The following criteria were considered in the installation of the HVS as far as practicable: -
    - (i) A horizontal platform with appropriate support to secure the sampler against gusty wind was provided.
    - (ii) Two samplers should not be placed less than 2m apart from each others;

- (iii) The distance between the HVS and any obstacles, such as buildings, was at least twice the height that the obstacle protrudes above the HVS.
- (iv) A minimum of 2 meters separation from walls, parapets and penthouse for rooftop sampler.
- (v) A minimum of 2 meters separation from any supporting structure, measured horizontally is required.
- (vi) No furnace or incinerator flues nearby.
- (vii) Airflow around the sampler was unrestricted.
- (viii) The sampler was located more than 20 meters from any dripline.
- (ix) Any wire fence and gate, required to protect the sampler, did not obstruct the monitoring process.
- (x) Permission was obtained to set up the samplers and access to the monitoring station.
- (xi) A secured supply of electricity was obtained to operate the sampler.
- (b) Preparation of Filter Papers
  - (i) Glass fibre filters, G810 were labelled and sufficient filters that were clean and without pinholes were selected.
  - (ii) All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than ±3 °C; the relative humidity (RH) was < 50% and not variable by more than ±5%. A convenient working RH was 40%.
  - (iii) All filter papers were prepared and analysed by ALS Technichem (HK) Pty Ltd., which is a HOKLAS accredited laboratory and has comprehensive quality assurance and quality control programmes.
- (c) Field Monitoring
  - (i) The power supply was checked to ensure the HVS works properly.
  - (ii) The filter holder and the area surrounding the filter were cleaned.
  - (iii) The filter holder was removed by loosening the four bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully.
  - (iv) The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter.
  - (v) The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied was sufficient to avoid air leakage at the edges.
  - (vi) Then the shelter lid was closed and was secured with the aluminium strip.
  - (vii) The HVS was warmed-up for about 5 minutes to establish run-temperature conditions.
  - (viii) A new flow rate record sheet was set into the flow recorder.
  - (ix) On site temperature and atmospheric pressure readings were taken and the flow rate of the HVS was checked and adjusted at around 1.3 m<sup>3</sup>/min, and complied with the range specified in the EM&A Manual (i.e. 0.6-1.7 m<sup>3</sup>/min).
  - (x) The programmable digital timer was set for a sampling period of 24 hrs, and the starting time, weather condition and the filter number were recorded.
  - (xi) The initial elapsed time was recorded.
  - (xii) At the end of sampling, on site temperature and atmospheric pressure readings were taken and the final flow rate of the HVS was checked and recorded.
  - (xiii) The final elapsed time was recorded.
  - (xiv) The sampled filter was removed carefully and folded in half length so that only surfaces with collected particulate matter were in contact.
  - (xv) It was then placed in a clean envelope and sealed.
  - (xvi) All monitoring information was recorded on a standard data sheet.
  - (xvii) Filters were then sent to ALS Technichem (HK) Pty Ltd. for analysis.
- (d) Maintenance and Calibration
  - (i) The HVS and its accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.

- (ii) HVSs were calibrated using TE-5025A Calibration Kit upon installation and thereafter at bi-monthly intervals.
- (iii) Calibration certificate of the TE-5025A Calibration Kit and the HVSs are provided in **Appendix E**.
- 3.1.7 1-hour TSP Monitoring
  - (a) Measuring Procedures

The measuring procedures of the 1-hour dust meter are in accordance with the Manufacturer's Instruction Manual as follows:

- (i) Turn the power on.
- (ii) Close the air collecting opening cover.
- (iii) Push the "TIME SETTING" switch to [BG]
- (iv) Push "START/STOP" switch to perform background measurement for 6 seconds.
- (v) Turn the knob at SENSI ADJ position to insert the light scattering plate.
- (vi) Leave the equipment for 1 minute upon "SPAN CHECK" is indicated in the display.
- (vii) Push "START/STOP" switch to perform automatic sensitivity adjustment. This measurement takes 1 minute.
- (viii) Pull out the knob and return it to MEASURE position.
- (ix) Push the "TIME SETTING" switch the time set in the display to 3 hours.
- (x) Lower down the air collection opening cover.
- (xi) Push "START/STOP" switch to start measurement.
- (b) Maintenance and Calibration
  - The 1-hour TSP meter was calibrated at 1-year intervals against a continuous particulate TEOM Monitor, Series 1400ab. Calibration certificates of the Laser Dust Monitors are provided in Appendix E.

## Monitoring Schedule for the Reporting Month

3.1.8 The schedule for environmental monitoring in November 2021 is provided in Appendix F.

## 3.2 Construction Noise Monitoring

#### Monitoring Requirements

3.2.1 In accordance with the EM&A Manual, impact noise monitoring should be conducted for at least once a week during the construction phase of the Project. **Table 3.3** summarises the monitoring parameters, frequency and duration of impact noise monitoring. The Action and Limit level of the noise monitoring is provided in **Appendix D**.

## Table 3.3Noise Monitoring Parameters, Frequency and Duration

Parameter and Duration	Frequency
30-mins measurement at each monitoring station between 0700 and 1900 on normal weekdays. Leq, L <sub>10</sub> and L <sub>90</sub> would be recorded.	At least once per week

#### Monitoring Equipment

3.2.2 Noise monitoring was performed using sound level meter at each designated monitoring station. The sound level meters deployed comply with the International Electrotechnical Commission Publications (IEC) 651:1979 (Type 1) and 804:1985 (Type 1) specifications. Acoustic calibrator was deployed to check the sound level meters at a known sound pressure level. Brand and model of the equipment is given in **Table 3.4**.

## Table 3.4 Noise Monitoring Equipment for Regular Noise Monitoring

Equipment	Brand and Model
Integrated Sound Level Meter	Model No. B&K 2270 (S/N: 2644597) Model No. B&K 2250-L (S/N: 2681366)
Acoustic Calibrator	Model No. MVI CAL21 (S/N: 34113610(2011)) Model No. B&K 4231 (S/N:3006428)

#### Monitoring Locations

3.2.3 The monitoring station for construction noise monitoring pertinent to the Project has been identified based on the approved EM&A Manual for SCL (HUH-ADM) of the Project. Location of the noise monitoring station is summarised in **Table 3.5** and shown in **Figure 3.1**.

Table 3.5	Noise Monitoring Station during Construction Phase
-----------	--

Identification No.	District	Alternative Noise Monitoring Location
M1a <sup>1</sup>	Wan Chai	Footbridge for Ex-Harbour Road Sports Centre

Remark:

 According to the updated site layout of CEDD Entrusted Works and Updated EM&A Manual for EP-376/2009 and EP-364/2009, Footbridge for Ex-Harbour Road Sports Centre (M1a) was selected as the most affected sensitive receiver during the construction phase.

#### Monitoring Methodology

- 3.2.4 Monitoring Procedure
  - (a) Façade measurements were made at M1a.
  - (b) The battery condition was checked to ensure the correct functioning of the meter.
  - (c) Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
    - (i) frequency weighting: A
    - (ii) time weighting: Fast

- (iii) time measurement: L<sub>eq(30-minutes)</sub> during non-restricted hours i.e. 0700 1900 on normal weekdays.
- (d) Prior to and after each noise measurement, the meter was calibrated using the acoustic calibrator for 94 dB(A) at 1000 Hz. If the difference in the calibration level before and after measurement was more than 1 dB(A), the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.
- (e) During the monitoring period, the  $L_{eq}$ ,  $L_{10}$  and  $L_{90}$  were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- (f) Noise measurement was paused during periods of high intrusive noise (e.g. dog barking, helicopter noise) if possible. Observations were recorded when intrusive noise was unavoidable.
- (g) Noise monitoring was cancelled in the presence of fog, rain, wind with a steady speed exceeding 5m/s, or wind with gusts exceeding 10m/s.
- 3.2.5 Maintenance and Calibration
  - (a) The microphone head of the sound level meter was cleaned with soft cloth at regular intervals.
  - (b) The meter and calibrator were sent to the supplier or HOKLAS laboratory to check and calibrate at yearly intervals.
  - (c) Calibration certificates of the sound level meters and acoustic calibrators are provided in **Appendix E**.

## Monitoring Schedule for the Reporting Month

3.2.6 The schedule for environmental monitoring in November 2021 is provided in Appendix F.

## 4 IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

4.1.1 The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Reports, the EP and EM&A Manuals. The implementation status of the environmental mitigation measures during the reporting period is summarized in **Appendix C.** Status of required submissions under the EP during the reporting period is summarised in **Table 4.1**.

## Table 4.1 Status of Required Submission under Further Environmental Permit

EP Condition	Submission	Submission Date
Condition 3.3 (FEP-13//364/2009/H & FEP-03/376/2009)	Monthly EM&A Report for October 2021	12 November 2021

## 5 MONITORING RESULTS

#### 5.1 Construction Dust Monitoring

5.1.1 The monitoring results for 24-hour TSP and 1-hour TSP are summarised in **Table 5.1** and **Table 5.2** respectively. Detailed air quality monitoring results and wind monitoring data extracted from the nearest Automatic Weather Station are presented in **Appendix G**.

Table 5.1 Summary of 24-mour For Momilloring Result in the Reporting Period	Table 5.1	Summary of 24-hour TSP Monitoring Result in the Reporting Period
---	-----------	--

ID	Average (μg/m³)	Range (µg/m³)	Action Level (μg/m³)	Limit Level (µg/m³)
CMA5b	66.2	54.7 – 87.4	209.9	260
CMA6a	33.2	23.7 – 43.9	207.1	260

Table 5.2 Summary of 1-hour TSP Monitoring Result in the Reporting Period

ID	Average (μg/m <sup>3</sup> )	Range (µg/m³)	Action Level (μg/m³)	Limit Level (µg/m³)
CMA5b	65.0	60.9 - 68.8	339.7	500
CMA6a	61.7	58.5 – 64.1	333	500

- 5.1.2 No Action and Limit Level exceedance were recorded for 1-hour TSP monitoring at the monitoring locations in the reporting month.
- 5.1.3 No Action and Limit Level exceedance were recorded for 24-hour TSP monitoring at the monitoring locations in the reporting month.
- 5.1.4 The event and action plan is annexed in **Appendix I**.
- 5.1.5 Major dust sources during the monitoring included construction dust, nearby traffic emission and other nearby construction sites.

#### 5.2 Regular Construction Noise Monitoring

5.2.1 The monitoring results for noise are summarized in **Table 5.3** and the monitoring data is provided in **Appendix H**.

## Table 5.3 Summary of Construction Noise Monitoring Results in the Reporting Period

ID	Range, dB(A), L <sub>eq (30 mins)</sub>	Limit Level, dB(A), L <sub>eq (30 mins)</sub>	
M1a <sup>(*)</sup>	<baseline< td=""><td>75</td></baseline<>	75	

(\*) Baseline correction will be made to the measured  $L_{eq}$  when the measured noise level exceeded the corresponding baseline noise level and presented in the table.

- 5.2.2 No Action Level exceedance was recorded since no noise related complaint was received in the reporting month.
- 5.2.3 No Limit Level exceedance of noise was recorded at the monitoring station in the reporting month.
- 5.2.4 The event and action plan is annexed in **Appendix I**.
- 5.2.5 Major noise sources during the monitoring included construction noise from the Project site, nearby traffic noise and the community.

## 5.3 Waste Management

- 5.3.1 C&D materials and wastes sorting were carried out on site. Receptacles were available for C&D wastes and general refuse collection.
- 5.3.2 As advised by the Contractor, 196 m<sup>3</sup> of inert C&D material was generated and disposed of as public fill in the reporting month. No inert C&D materials were reused in other projects or in the Contract in the reporting month. No fill material was imported in the reporting month. No general refuse was generated in the reporting month. No metal, paper/cardboard packaging material, plastic was collected by recycling contractor in the reporting month. No chemical waste was collected by licensed contractor in the reporting period. No Type 1 and Type 2 of Marine sediment were disposed of at Confined Marine Disposal Facility to the East of Sha Chau. The waste flow table is annexed in **Appendix K**.
- 5.3.3 The Contractor is advised to properly maintain on site C&D materials and wastes collection, sorting and recording system and maximize reuse / recycle of C&D materials and wastes. The Contractor is reminded to properly maintain the site tidiness and dispose of the wastes accumulated on site regularly and properly.
- 5.3.4 The Contractor is reminded that chemical waste containers should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes

## 5.4 Landscape and Visual

5.4.1 Weekly inspection of the implementation of landscape and visual mitigation measures was conducted. A summary of the site inspection is provided in **Appendix C**. The observations and recommendations made during the site inspections are presented in **Table 6.1**.

#### **ENVIRONMENTAL SITE INSPECTION AND AUDIT** 6

- 6.1.1 Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. A summary of the mitigation measures implementation schedule is provided in Appendix C.
- 6.1.2 In the reporting month, 4 site inspection were carried out on 4, 11, 19 and 25 November 2021. Joint inspections with the IEC, ER, the Contractor and the ET were conducted on 19 November 2021. No non-compliance was recorded during the site inspection. Details of observations recorded during the site inspections are presented in Table 6.1.

Table 6.	1 Observat	ions and Recommendations of Site Audit	
Parameters	Date	Observations and Recommendations	Follow-up
Air Quality	19 Nov 2021	<ul> <li><u>Reminder</u></li> <li>The haul road was observed dry. The contractor was reminded to provide watering for haul road, leaving vehicles and dusty materials at W22 for preventing dust emission.</li> </ul>	This item was rectified on 25 Nov 2021.
	25 Nov 2021	• Open stockpile was observed at W22. The Contractor should provide proper cover to prevent dust emission.	This item was rectified on 30 Nov 2021.
Noise	Nil	Nil	Nil
Water Quality	Nil	Nil	Nil
Waste/ Chemical	11 Nov 2021	Reminder • Accumulated refuse was observed at W22. The Contractor was reminded to clean the refuse regularly.	This item was rectified on 19 Nov 2021.
Management	25 Nov 2021	Reminder • The Contractor was reminded to clean the refuse regularly at W22.	This item was rectified on 30 Nov 2021.
Landscape & Visual	Nil	Nil	Nil
Permits/ Licenses	Nil	Nil	Nil

e 6.1	Observations and Recommendations of Site Audit	

6.1.3 No follow up action was requested by Contractor's ET during the site inspection on 4 November 2021.

## 7 ENVIRONMENTAL NON-CONFORMANCE

#### 7.1 Summary of Monitoring Exceedances

- 7.1.1 All 24-hour TSP result was below the Action and Limit level at all monitoring locations in the reporting month.
- 7.1.2 All 1-hour TSP result was below the Action and Limit level at all monitoring locations in the reporting month
- 7.1.3 No Action Level exceedance was recorded since no noise related complaint was received in the reporting month.
- 7.1.4 No Limit Level exceedance for noise was recorded at all monitoring stations in the reporting month.

## 7.2 Summary of Environmental Non-Compliance

7.2.1 No environmental non-compliance was recorded in the reporting month.

#### 7.3 Summary of Environmental Complaints

7.3.1 No environmental related complaint was received in the reporting month. Cumulative statistics on environmental complaints is provided in **Appendix J**.

## 7.4 Summary of Environmental Summon and Successful Prosecutions

7.4.1 No environmental related prosecution or notification of summons was received in the reporting month. Cumulative statistics on notification of summons and successful prosecutions is provided in **Appendix J**.

## 8 FUTURE KEY ISSUES

## 8.1 Construction Programme for the Next Three Month

0 4 4	$-\mathbf{T}$ ( $\mathbf{x}$ , $\mathbf{y}$ ,	D		00 11 1
8.1.1	The major construction works between	December 2021	and February 20	22 will be:

Location	Site Activities
Road P2 –	Underground Drainage
West (Slip Road 3)	Road works
Road P2 –	Drainage works
East (Hung Hing Road)	Underground Utilities
	Road works (TTM)
Road P2 – PTI	Drainage & UU works
(Public Transport	Road works (TTM)
Interchange)	Footpath pavement
	Relocation of temporary PTI

## 8.2 Key Issues for the Coming Month

8.2.1 Potential environmental impacts arising from the above construction activities are mainly associated with construction dust, construction noise, water quality and waste management.

## 8.3 Monitoring Schedule for the Next Three Month

8.3.1 The tentative schedules for environmental monitoring in between December 2021 to February 2022 are provided in **Appendix F**.

## 9 CONCLUSIONS AND RECOMMENDATIONS

## 9.1 Conclusions

- 9.1.1 24-hour TSP, 1-hour TSP and noise monitoring were carried out in the reporting month.
- 9.1.2 No Action and Limit Level exceedance was recorded for 24-hour TSP monitoring at the monitoring locations in the reporting month.
- 9.1.3 No Action and Limit Level exceedance was recorded for 1-hour TSP monitoring at the monitoring locations in the reporting month
- 9.1.4 No Action Level exceedance was recorded since no noise related complaint was received in the reporting month.
- 9.1.5 No Limit Level exceedance for noise was recorded at all monitoring stations in the reporting month.
- 9.1.6 4 nos. of environmental site inspections were carried out in November 2021. Recommendations on remedial actions were given to the Contractor for the deficiencies identified during the site audit.
- 9.1.7 No environmental complaint was received in the reporting month.
- 9.1.8 No notification of summons and successful prosecution were received in the reporting month.
- 9.1.9 Referring to the Contractor's information, no notification of summons and successful prosecution was received in the reporting month.

## 9.2 Recommendations

9.2.1 According to the environmental site inspections performed in the reporting month, the following recommendations were provided: -

#### Air Quality Impact

• The contractor was reminded to provide regular water for the haul road and cover the stockpile of dusty materials to prevent dust emission.

#### Construction Noise Impact

• No specific observation was identified in the reporting month.

#### Water Quality Impact

• No specific observation was identified in the reporting month.

#### Chemical and Waste Management

The contractor was reminded to remove refuse regularly to maintain the cleanness of the site.


## Landscape & Visual Impact


• No specific observation was identified in the reporting month.

## Permits/licenses

• No specific observation was identified in the reporting month.

FIGURES

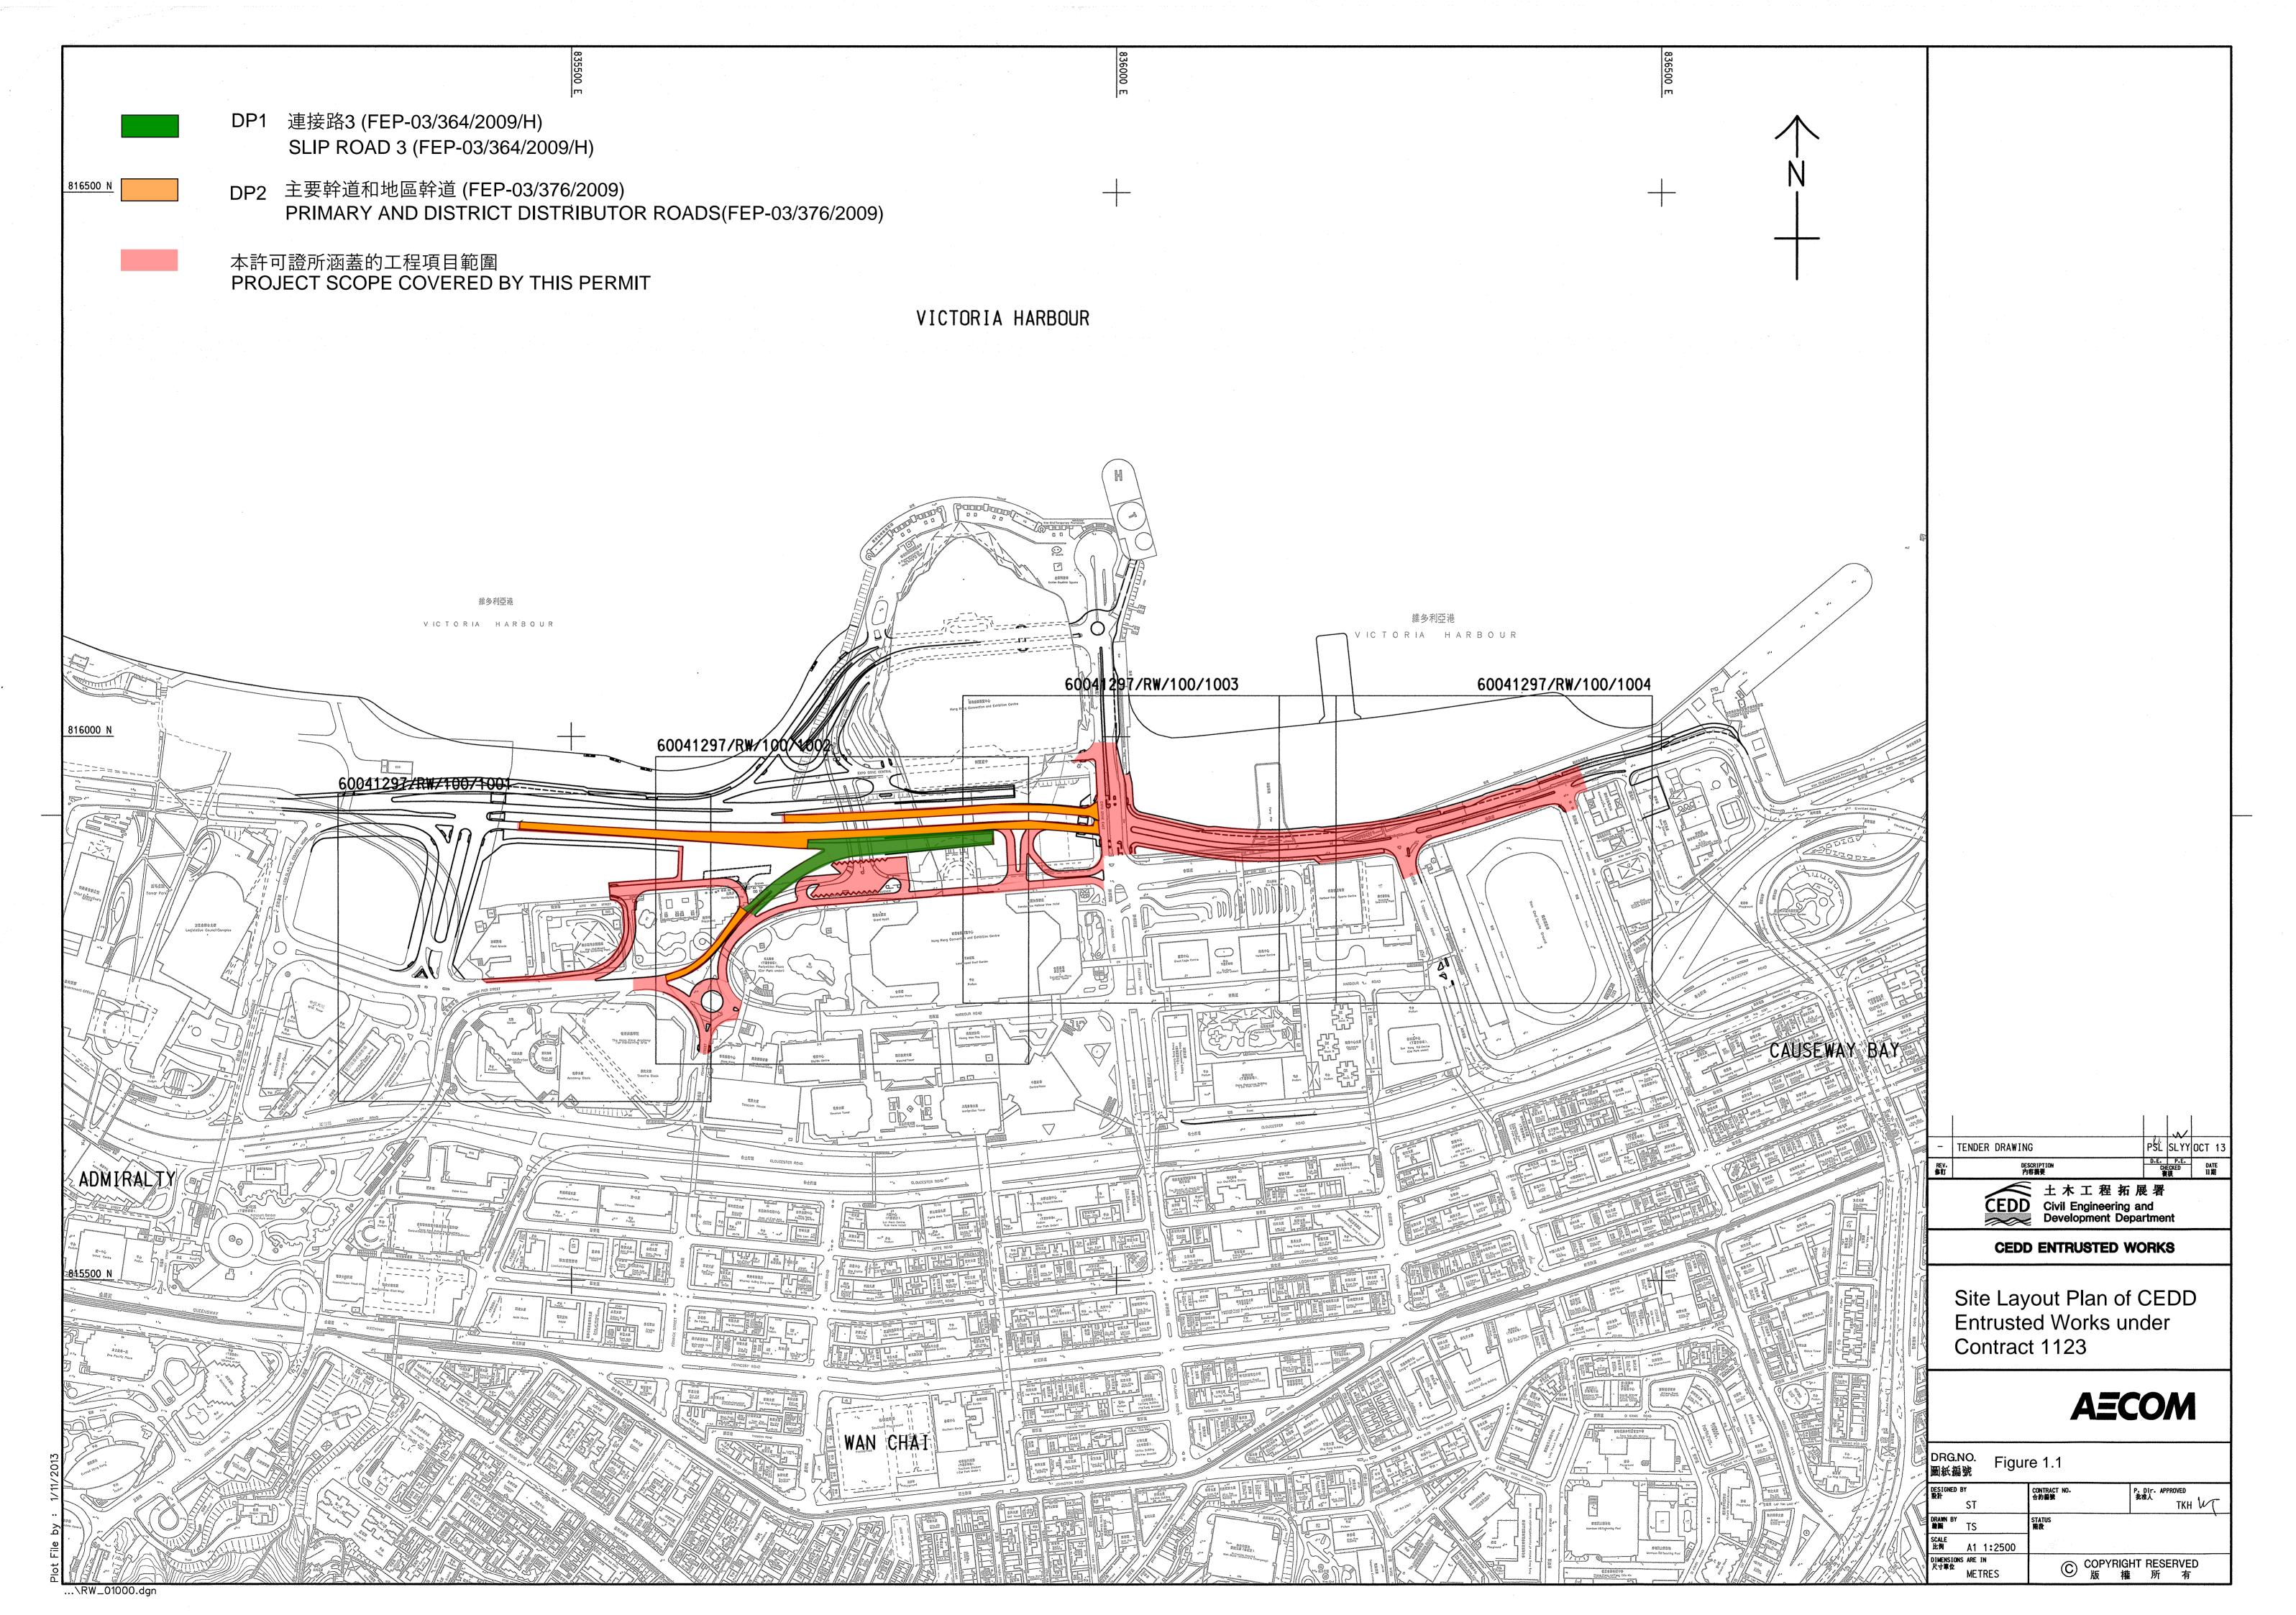

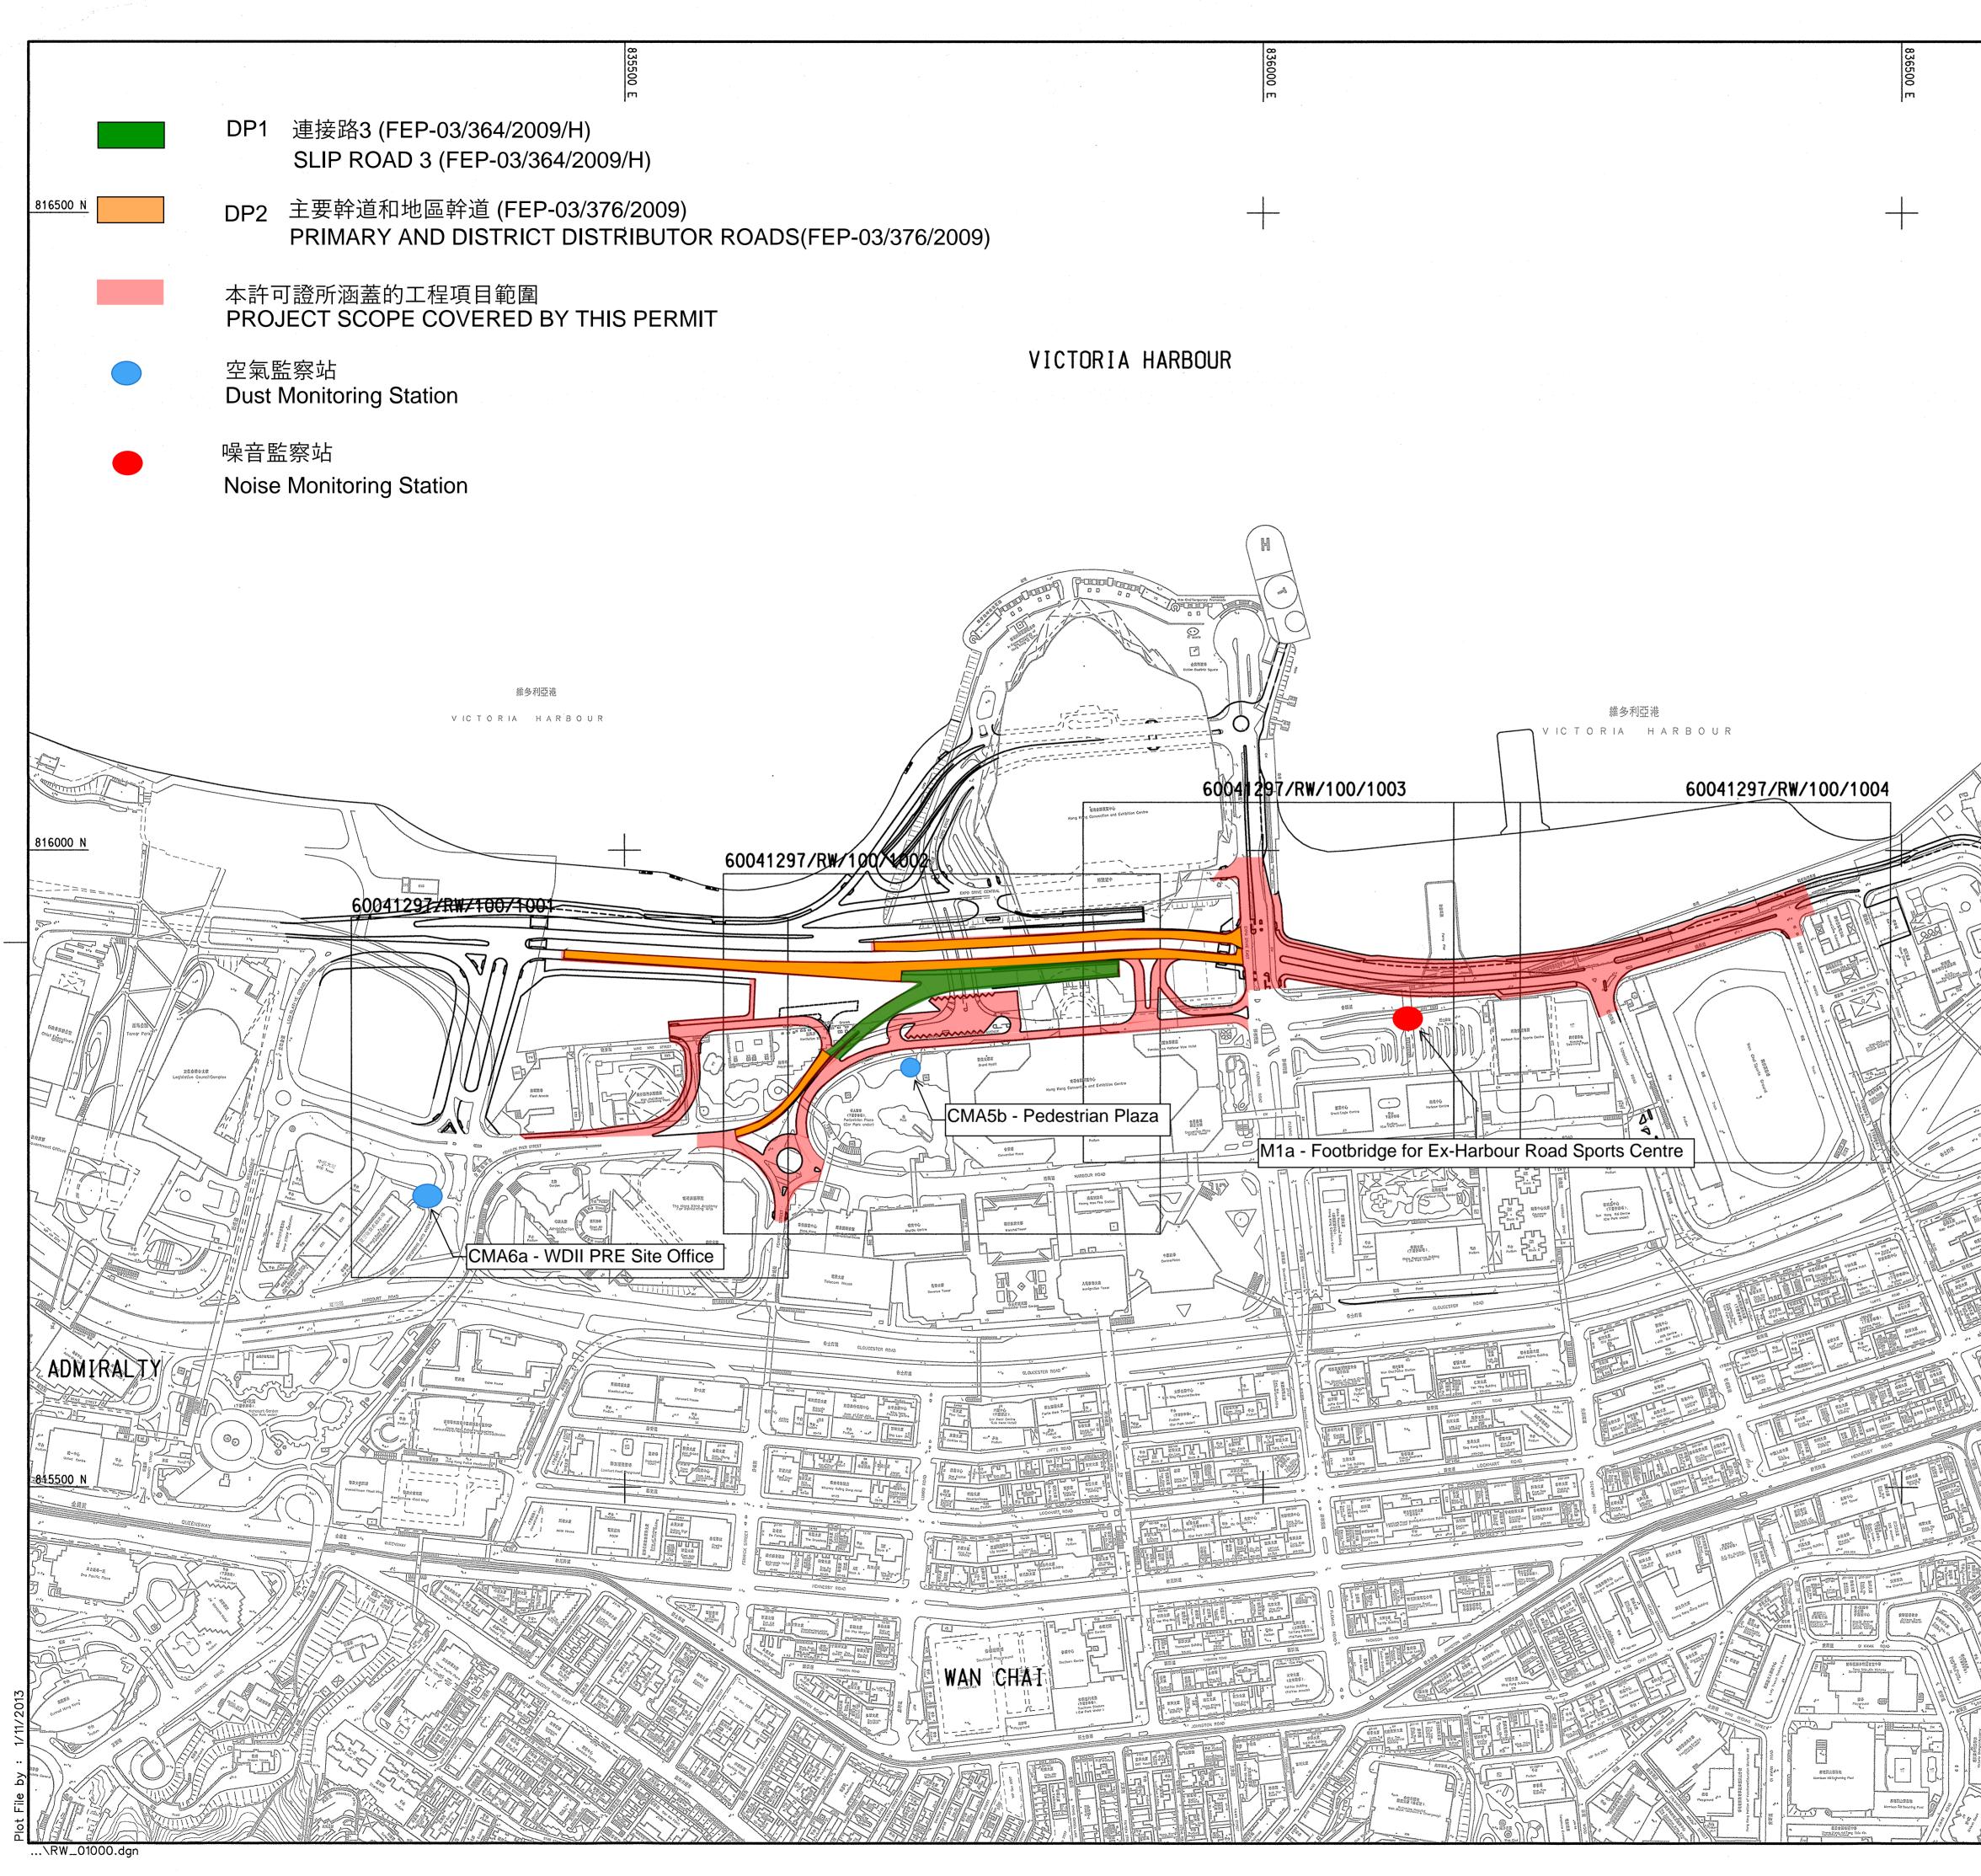

CAUSE WAY BAY	CEDD	D.E.     P.E.       改書     DATE       改書     日期
		and Noise Monitoring for CEDD Entrusted
	DRG.NO. Figur 圖紙編號	CONTRACT NO. P. DIr. APPROVED
	ST DRAWN BY 新聞 TS SCALE 此例 A1 1:2500 DIMENSIONS ARE IN 尺寸単位	TKH W (
	R · · 单位 METRES	C COPYRIGHT RESERVED 版 權 所 有

APPENDIX A

**Construction Programme** 

	isk Name	Duration	Start	Finish Dec	Jan	an Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct No
C	EDD Entrusted works- Road P2- Slip Road 3	785 d?	Jan 7 '20	Aug 3 '22		
	SR3- TTM 1	457 d	Jan 7 '20	Jul 13 '21		
	SR3- TTM 1.2 -Coach Park Area:	36 d	Jun 1 '21	Jul 13 '21		
	Construct the gullies and drain -Assumed( after Area B backfill and		Jun 1 '21	Jun 28 '21		Construct the gullies and drain -Assumed( after Area B backfill and E37/E28 Completion)
	Backfill and reinstate temp pavement		Jun 29 '21	Jul 13 '21		Backfill and reinstate temp pavement
	SR3- TTM 2a	_	May 28 '20	May 10 '21		
	Interface with WDII		Aug 22 '20	Feb 16 '21		
	Handover P6B & P6C and P6E		Feb 16 '21	Feb 16 '21		Handover P6B & P6C and P6E
	SR3 TTM 2a.2 – Slip Road 3 and Coach parking area		May 30 '20	May 10 '21		
	Construct watermain F19 tee and fire hydrant		Jan 25 '21	Feb 6 '21		Construct watermain F19 tee and fire hydrant
	Construct part of irrigation main and pipe sleeve for WP7-2		Feb 8 '21	Feb 13 '21	-	Construct part of irrigation main and pipe sleeve for WP7-2
	Construct kerbline and footpath pavement		Feb 15 '21	Apr 10 '21		Construct kerbline and footpath pavement
	Remove & Re-construct asphalt pavement for Slip Road 3 and		Apr 12 '21	May 10 '21		Remove & Re-construct asphalt pavement for Slip Road 3 and Convention Avenue W/B
	SR3 TTM 2a.3 – Reboundout-Planter No. 3		Dec 24 '20	Feb 20 '21		
	Construction the permanent traffic island at southside		Jan 25 '21	Feb 20 '21		Construction the permanent traffic island at southside
	SR3 TTM 2b.2 –Permanent Slip Road 3 construction (2nd portion)		Jan 22 '21	Jun 18 '21	-	
	· · · · ·		Jan 22 '21	Mar 4 '21		Construct drainage
	Construct drainage Construct watermain F17		Mar 5 '21	Apr 1 '21		Construct watermain F17
	Construct watermain F17		Apr 2 '21	Apr 29 '21		Construct gantry foundation
	Construct road kerb & central divider		Apr 2 21 Apr 30 '21	May 21 '21		Construct road kerb & central divider
	Construct asphalt pavement		May 22 '21	Jun 4 '21		Construct asphalt pavement
	Construct temp street light		Jun 5 '21	Jun 18 '21		Construct temp street light
	SR3 TTM 2b.3 -Temp Road (Temp LungKing Street)		Jun 19 '21	Jul 17 '21		
	Construct temp. road		Jun 19 '21	Jul 3 '21		Construct temp. road
	Construct temp street light	12 d		Jul 17 '21		Construct temp street light
	SR3- TTM 3		Feb 20 '21	Dec 30 '21		
	Interface with WDII		Aug 12 '21	Aug 12 '21		♦ Interface with WDII
	Handover P6		•	-		Handover P6
			Aug 12 '21	Aug 12 '21		
	SR3 TTM 3.1: Divert CEB to Permanent Slip Road 3		Apr 9 '21	Jul 21 '21		Preparation woks for divert CWB traffic to Slip Road 3
	Preparation woks for divert CWB traffic to Slip Road 3		Apr 9 '21	Jul 5 '21		Divert CWB traffic to Slip Road 3
	Divert CWB traffic to Slip Road 3		Jul 19 '21	Jul 21 '21	_	
	SR3 TTM 3.2: Close Detoured Slip Road 3		Jul 22 '21	Jul 24 '21		Close Detoured Slip Road 3
	Close Detoured Slip Road 3		Jul 22 '21	Jul 24 '21		
	SR3 TTM 3.3: Temp lungKing Road		Jul 26 '21	Jul 28 '21		
	Divert Traffic to Temp. Lung King Road		Jul 26 '21	Jul 28 '21		Divert Traffic to Temp. Lung King Road
	SR3 TTM 3.4 -Reboundout		Jul 22 '21	Nov 25 '21	_	
	De-commission of traffic light system and change to free flow road		Jul 22 '21	Jul 28 '21		De-commission of traffic light system and change to free flow road junction
	Construct drainage		Jul 29 '21	Sep 22 '21		Construct drainage
	Construct irrigation main		Sep 23 '21	Oct 7 '21	_	Construct irrigation main
	Construct permanent planters		Oct 8 '21	Nov 11 '21		Construct permanent planters
	construction of Rest of the Traffic Island at Harbour Road		Nov 12 '21	Nov 25 '21		construction of Rest of the Traffic Island at Harbour Road
	SR3 TTM 3.5 -LungKing Street		Feb 20 '21	Dec 30 '21	_	A Land W22 Access
	Land W22 Access		Feb 20 '21	Feb 20 '21	_	Land W22 Access
	Land W21 Access		Feb 20 '21	Feb 20 '21	_	Land W21 Access      Temp Road Diversion of existing MVB(CWB) EVA
	Temp Road Diversion of existing MVB(CWB) EVA		Mar 26 '21	Apr 22 '21		
	Construct Part (bay 1-4) retaining wall and drainage/lighting duct		Apr 23 '21	Oct 18 '21		Construct Part (bay 1-4) retaining wall and drainage/lighting duct
	Construct remaining retaining wall		Jul 29 '21	Sep 22 '21		Construct remaining retaining wall Construct remaining drainage
	Construct remaining drainage		Sep 23 '21	Nov 18 '21		Construct site formation and road kerb
	Construct site formation and road kerb		Nov 19 '21 Dec 10 '21	Dec 9 '21 Dec 30 '21		Construct site formation and road kerb
	Construct asphalt road pavement and footpath					
	SR3- TTM 4 1 Dehoundout		Nov 26 '21	Mar 11 '22		
	SR3 TTM 4.1 -Reboundout		Nov 26 '21	Dec 2 '21		Divert the Traffic to outmost lanes
	Divert the Traffic to outmost lanes		Nov 26 '21	Dec 2 '21	_	
	SR3 TTM 4.2 - Lung King Street/Fenwick Pier Street		Dec 31 '21	Mar 11 '22	_	Construct drainage & gully
	Construct drainage & gully		Dec 31 '21	Feb 11 '22		
	Construct Footpath		Feb 12 '22	Mar 11 '22		Construct Footpath
	SR3- TTM 5		Jul 22 '21	Dec 13 '21	_	
	Interface with WDII		Nov 12 '21	Nov 12 '21		Interface with WDII
	Handover Land- P5		Nov 12 '21	Nov 12 '21		♦ Handover Land- P5
	SR3 TTM 5.1 -Temp Road Diversion for Lung Wo Road		Jul 22 '21	Sep 15 '21		
	Temp Road Construction TTM Diversion		Jul 22 '21	Aug 18 '21	_	Temp Road Construction
		h NC	Aug 19 '21	Sep 15 '21		TTM Diversion

CONTRACT NO.SCL1123

Shatin to Central Link Contract 1123- Exhibition Station and Western Approach Tunnel

## **CEDD Entrusted Works**

Page 1

00	Task Name	Duration	Start	Finish	Dec	2021 Jan	Ech	Mar Apr May	lue	Jul	Aug	Son	Oct New	Dec	2022 Jan	Feb	Mar	
88	SR3 TTM 5.2 - Re-alignment Lung Wo Road(W/B)	60 d	Sep 16 '21	Nov 25 '21		Jg[]	гер	ινιαι Αμι Μαγ	Jun	JUI	Aug	зер		Dec	Jall	reb	IVIDI	+
89	Reconstruct drainage and Gullies	36 d	Sep 16 '21	Oct 28 '21									Recon	struct drai	nage and	Gullies		
90	Reconstruct Road kerb and Pavement	24 d	Oct 29 '21	Nov 25 '21										•	ruct Road			er
91	Removal of De-toured Slip Road 3		Oct 29 '21	Nov 25 '21										Removal	l of De-to	ured Slip	א Road 3	_
92	SR5 TTM 5.3 -Reconstruct kerbline and Pavement between Lung		Sep 16 '21	Dec 13 '21														
93	<ul> <li>Reconstruct kerbline and Pavement between Lung Wo road (w/b) &amp;</li> </ul>		Sep 16 '21	Dec 13 '21										-Re	econstruc	t kerblin	ie and Pa	V
94	SR3- TTM 6		Feb 22 '21	Aug 3 '22														_
95	SR3 TTM 6.1 - Lung Wo Road North		Nov 26 '21	Aug 3 '22	-													_
96	Divert traffic to South side of Lung Wo Road		Nov 26 '21	Dec 2 '21	-									Divert	traffic to	South si	de of Lur	g
97 98	Drainage and raod works at North side	108 d		Apr 8 '22	-		_		_					-		+		-
98 99	Removal of Temp Road Reinstatement of Planter Area	24 d	Apr 9 '22 May 7 '22	May 6 '22 Aug 3 '22	-													-
100	SR3 TTM 6.2 - Abandoned Lung King Street		Feb 22 '21	Feb 8 '22														-
101	Removal and abondoned Lung King Street		Dec 14 '21	Feb 8 '22											<u> </u>	Rem	noval and	Ē
102			Feb 22 '21	Feb 22 '21														-
	Removal of Temp Slip Road		Sep 21 '20	Mar 30 '21											-		-	-
128	Removal of Temp Slip Road		Jan 16 '21	Feb 1 '21			Remov	val of Temp Slip Road									-	-
129	Trimming D-wall Panels(L92-L101& L34-L37)	20 d		Feb 24 '21				Trimming D-wall Panels(L	92-L101& L	34-L37)				_	1		-	+
130	Continue rest Drainage and sewage construction	24 d	Feb 25 '21	Mar 24 '21				Continue rest Dra	inage and	sewage	constructi	on					-	1
131	No fine Concrete Backfill	5 d	Mar 25 '21	Mar 30 '21				No fine Concre	e Backfill									1
132	B400 (EVA)	54 d	Feb 25 '21	Apr 28 '21	·													
133	Complete Remaining Drainage		Feb 25 '21	Mar 24 '21	-			Complete Remai	-	-								
134	Site Formation/Road Kerb/Pedestrian Crossing		Mar 25 '21	Apr 14 '21				Site Forma				rossing						_
135	Road works and EVA ready		Apr 15 '21	Apr 28 '21				Road v	orks and E	VA read	/			_				_
	B300	104 d		Jun 2 '21					(000)/0									_
137	Close Area C1 opening (DRD)/Backfill		Feb 1 '21	Mar 13 '21				Close Area C1 openi Break D-w			Complet	o Romai	ning dringgo					_
138 139	Break D-wall (L90-91& L32-33)Complete Remaining drinage		Mar 15 '21	Apr 15 '21				Comple	-		Complet	e Keman	ning unnage					_
139 140	Complete Remaining UU Site Formation/Road Kerb/Pedestrian Crossing		Apr 16 '21 Apr 28 '21	Apr 27 '21 May 19 '21					Site Format		d Kerb/Pe	destrian	Crossing	_				-
140 141	Final Road works and Road marking		May 20 '21	Jun 2 '21					Final Ro									-
142	CEDD Entrusted works-Road P2- Hung Hing Road		Jul 29 '20	May 25 '22									-0					+
143			Jul 29 '20															_
143	TTM1-Divert Convention Avenue and Hung Hing Road		Jui 29 20 Nov 4 '20	May 29 '21 May 29 '21														-
150	TTM1-Road works at Convention Avenue and Hung Hing Road Underground Drinage and Utilities		Nov 25 '20	Mar 12 '21				Underground Drinag	e and Utilit	ies				_	+			_
150 151	Permanent Road Formation		Feb 20 '21	Apr 2 '21				Permanent Ro										-
152	Permanent Road pavement and Footpath	24 d		Apr 30 '21					nent Road		nt and Fo	otpath			1			+
153	Interface transition pavement works		May 3 '21	May 29 '21					Interface	transiti	on pavem	ent work	s		+			-
	TTM2-Divert East direction to permanent alignment		, Mar 31 '21	Nov 2 '21														-
154	This biver Last an ection to permanent angiment			Jun 26 '21	-					Constuct	Temp roa	ad					_	-
	Constuct Temp road	24 d	May 31 '21	JUII ZO ZI	•													T
155			May 31 '21 Mar 31 '21	Jun 26 '21						Apply TT	M and Ap	proval						_
155 156	Constuct Temp road	75 d	-								M and Ap lement TT				<u> </u>			_
155 156 157	Constuct Temp road Apply TTM and Approval	75 d 12 d	Mar 31 '21	Jun 26 '21							-							_
155 156 157 158 159	Constuct Temp road Apply TTM and Approval Implement TTM2 <b>TTM2- Drainage and road works at Junctions</b> Underground Drinage and Utilities	75 d 12 d <b>96 d</b> 48 d	Mar 31 '21 Jun 28 '21 <b>Jul 13 '21</b> Jul 13 '21	Jun 26 '21 Jul 12 '21 <b>Nov 2 '21</b> Sep 6 '21	- - -						-	M2 Under	rground Drinage		es			
155 156 157 158 159 160	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb	75 d 12 d <b>96 d</b> 48 d 18 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Jul 13 '21 Aug 31 '21	Jun 26 '21 Jul 12 '21 <b>Nov 2 '21</b> Sep 6 '21 Sep 20 '21	- -						-	M2 Under	te Formation/Ro	oad Kerb				
154 155 156 157 158 159 160 161	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions	75 d 12 d <b>96 d</b> 48 d 18 d 18 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21	Jun 26 '21 Jul 12 '21 <b>Nov 2 '21</b> Sep 6 '21 Sep 20 '21 Oct 12 '21	- - - -						-	M2 Under	te Formation/Ro	oad Kerb Road wor	ks at Junc			
155 156 157 158 159 160 161 162	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works	75 d 12 d <b>96 d</b> 48 d 18 d 18 d 18 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21	Jun 26 '21 Jul 12 '21 <b>Nov 2 '21</b> Sep 6 '21 Sep 20 '21 Oct 12 '21 Nov 2 '21	- - - -						-	M2 Under	te Formation/Ro	oad Kerb	ks at Junc		orks	
155 156 157 158 159 160 161 162 163	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road	75 d 12 d <b>96 d</b> 48 d 18 d 18 d 18 d <b>177 d</b>	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21	Jun 26 '21 Jul 12 '21 <b>Nov 2 '21</b> Sep 6 '21 Oct 12 '21 Nov 2 '21 <b>Mar 23 '22</b>							-	M2 Under	te Formation/Ro Permanent Inter	oad Kerb Road wor face transi	ks at Junc	ement wo	orks	
155 156 157 158 159 160 161 162 163 164	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road	75 d 12 d <b>96 d</b> 48 d 18 d 18 d <b>177 d</b> 18 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Nov 3 '21	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Nov 2 '21 Mar 23 '22 Nov 23 '21							-	M2 Under	te Formation/Ro Permanent Inter	oad Kerb Road wor face transi Constuct	ks at Junc ition pave Temp roa	ement wo		
155 156 157 158 159 160 161 162 163 164 165	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval	75 d 12 d <b>96 d</b> 48 d 18 d 18 d 18 d <b>177 d</b> 18 d 75 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Aug 27 '21	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Oct 12 '21 Nov 2 '21 Mar 23 '22 Nov 23 '21 Nov 23 '21							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A	ement wo ad pproval		
155 156 157 158 159 160 161 162 163 163 164 165	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3	75 d 12 d 96 d 48 d 18 d 18 d 18 d 177 d 18 d 75 d 12 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Aug 27 '21 Nov 24 '21	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Mar 23 '22 Nov 23 '21 Nov 23 '21 Dec 7 '21							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct	ks at Junc ition pave Temp roa M3 and A	ement wo ad pproval		
155 156 157 158 159 160 161 162 163 164 165 166 166	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3 TTM3- Drainage and road works at Junctions	75 d 12 d 96 d 48 d 18 d 18 d 18 d 177 d 18 d 75 d 12 d 90 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Aug 27 '21 Nov 24 '21 Dec 8 '21	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Mar 23 '22 Nov 23 '21 Nov 23 '21 Dec 7 '21 Mar 23 '22							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A ement TT	ement wo ad pproval M3		
155 156 157 158 159 160 161 162 163 164 165 166 166 167	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3 TTM3- Drainage and road works at Junctions Underground Drinage and Utilities	75 d 12 d 96 d 48 d 18 d 18 d 177 d 18 d 75 d 12 d 90 d 36 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Aug 27 '21 Nov 24 '21 Dec 8 '21	Jun 26 '21 Jul 12 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Nov 2 '21 Mar 23 '22 Nov 23 '21 Dec 7 '21 Mar 23 '22 Jan 19 '22							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A ement TT	ement wo ad pproval M3 ndergrou	und Drin	_
155 156 157 158 159 160 161 162 163 164 165 166 167 168	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3 TTM3- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb	75 d 12 d 96 d 48 d 18 d 18 d 18 d 177 d 18 d 75 d 12 d 90 d 36 d 18 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Nov 3 '21 Nov 24 '21 Dec 8 '21 Jan 20 '22	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Nov 2 '21 Mar 23 '22 Nov 23 '21 Dec 7 '21 Mar 23 '22 Jan 19 '22 Feb 9 '22							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A ement TT	ement wo ad pproval M3 ndergroo		0
155 156 157 158 159 160 161 162 163 164 165 166 167 168 169 170	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3 TTM3- Drainage and road works at Junctions Underground Drinage and Utilities	75 d 12 d 96 d 48 d 18 d 18 d 18 d 177 d 18 d 75 d 12 d 90 d 36 d 18 d 18 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Aug 27 '21 Nov 24 '21 Dec 8 '21	Jun 26 '21 Jul 12 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Nov 2 '21 Mar 23 '22 Nov 23 '21 Dec 7 '21 Mar 23 '22 Jan 19 '22							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A ement TT	ement wo ad pproval M3 ndergroo	ound Drina	o an
155 156 157 158 159 160 161 162 163 164 165 166 167 168 169 170 171	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3 TTM3- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions	75 d 12 d 96 d 18 d 18 d 18 d 177 d 18 d 75 d 12 d 90 d 36 d 18 d 18 d 18 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Nov 3 '21 Nov 24 '21 Dec 8 '21 Jec 8 '21 Jan 20 '22 Feb 10 '22	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Oct 12 '21 Nov 2 '21 Mar 23 '22 Nov 23 '21 Dec 7 '21 Mar 23 '22 Jan 19 '22 Feb 9 '22 Mar 2 '22							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A ement TT	ement wo ad pproval M3 ndergroo	ound Drina e Formati Perma	o an
155 156 157 158 159 160 161 162 163 164 165 166 167	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3 TTM3- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works	75 d 12 d 96 d 18 d 18 d 18 d 177 d 18 d 75 d 12 d 90 d 36 d 18 d 18 d 18 d 18 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Nov 3 '21 Nov 24 '21 Nov 24 '21 Dec 8 '21 Jan 20 '22 Feb 10 '22 Mar 3 '22	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Nov 2 '21 Mar 23 '22 Nov 23 '21 Dec 7 '21 Mar 23 '22 Jan 19 '22 Feb 9 '22 Mar 2 '22							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A ement TT	ement wo ad pproval M3 ndergroo	ound Drina e Formati Perma	o ar Ir
155 156 157 158 159 160 161 162 163 164 165 166 167 168 169 170 171	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3 TTM3- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM4- Final Alignmeent	75 d 12 d 96 d 48 d 18 d 18 d 18 d 177 d 18 d 75 d 12 d 90 d 36 d 18 d 18 d 18 d 18 d 18 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Aug 27 '21 Aug 27 '21 Nov 24 '21 Dec 8 '21 Jan 20 '22 Feb 10 '22 Mar 3 '22 Dec 25 '21	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Nov 2 '21 Mar 23 '22 Nov 23 '21 Dec 7 '21 Mar 23 '22 Jan 19 '22 Feb 9 '22 Mar 2 '22 Mar 23 '22 May 25 '22							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A ement TT	ement wo ad pproval M3 ndergroo	e Formati	o ar Ir A
155 156 157 158 159 160 161 162 163 164 165 166 166 166 166 167 168 169 170 171 172	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3 TTM3- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM4- Final Alignmeent Apply TTM4 and Approval	75 d 12 d 96 d 18 d 18 d 18 d 177 d 18 d 75 d 12 d 90 d 36 d 18 d 18 d 18 d 18 d 18 d 18 d 18 d	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Aug 27 '21 Nov 24 '21 Nov 24 '21 Dec 8 '21 Jan 20 '22 Feb 10 '22 Mar 3 '22 Dec 25 '21	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Mar 23 '22 Nov 23 '21 Nov 23 '21 Dec 7 '21 Mar 23 '22 Mar 2 '22 Mar 23 '22 Mar 23 '22							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A ement TT	ement wo ad pproval M3 ndergroo	e Formati	oi an In A
155 156 157 158 159 160 161 162 163 164 165 166 166 167 168 169 170 171 172 173 174	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3 TTM3- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM4- Final Alignmeent Apply TTM4 and Approval Implement TM4	75 d 12 d 96 d 18 d 18 d 18 d 177 d 18 d 75 d 12 d 90 d 36 d 18 d 18 d 18 d 18 d 18 d 18 d 18 d 18	Mar 31 '21         Jun 28 '21         Jul 13 '21         Aug 31 '21         Aug 31 '21         Oct 13 '21         Aug 27 '21         Aug 27 '21         Aug 27 '21         Nov 3 '21         Aug 27 '21         Dec 8 '21         Jan 20 '22         Feb 10 '22         Mar 3 '22         Dec 25 '21         Mar 24 '22         Apr 14 '22         May 25 '22	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Mar 23 '22 Nov 23 '21 Nov 23 '21 Dec 7 '21 Mar 23 '22 Mar 23 '22 Mar 23 '22 Mar 23 '22 Mar 23 '22 Apr 13 '22							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A ement TT	ement wo ad pproval M3 ndergroo	e Formati	oi an In A
55 56 57 58 59 60 61 62 63 64 65 66 67 68 69 70 71 72 73 74 75 76	Constuct Temp road Apply TTM and Approval Implement TTM2 TTM2- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM3- Diversion on Marsh Road/HungHing Road Constuct Temp road Apply TTM3 and Approval Implement TTM3 TTM3- Drainage and road works at Junctions Underground Drinage and Utilities Site Formation/Road Kerb Permanent Road works at Junctions Interface transition pavement works TTM4- Final Alignmeent Apply TTM4 and Approval Implement TM4 Permanent Foot path and Central Island Construction	75 d 12 d 96 d 18 d 18 d 18 d 177 d 18 d 75 d 12 d 90 d 36 d 18 d 18 d 18 d 18 d 18 d 18 d 18 d 18	Mar 31 '21 Jun 28 '21 Jul 13 '21 Aug 31 '21 Sep 21 '21 Oct 13 '21 Aug 27 '21 Aug 27 '21 Nov 3 '21 Nov 24 '21 Dec 8 '21 Jan 20 '22 Feb 10 '22 Mar 3 '22 Dec 25 '21 Dec 25 '21 Mar 24 '22 Apr 14 '22	Jun 26 '21 Jul 12 '21 Nov 2 '21 Sep 6 '21 Sep 20 '21 Oct 12 '21 Mar 23 '22 Nov 23 '21 Nov 23 '21 Dec 7 '21 Mar 23 '22 Mar 23 '22 Mar 23 '22 Mar 23 '22 Mar 23 '22 Mar 23 '22 Mar 23 '22 Apr 13 '22 May 25 '22							-	M2 Under	te Formation/Ro	oad Kerb Road wor face transi Constuct Apply TTI	ks at Junc ition pave Temp roa M3 and A ement TT	ement wo ad pproval M3 ndergroo	e Formati	or an In

- CONTRACT NO.SCL1123 Shatin to Central Link
- Contract 1123- Exhibition Station and Western Approach Tunnel

## **CEDD Entrusted Works**

Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
nt								
ement be	etween L	ung Wo r	oad (w/b	) & CWB	Tunnel(V	V/B)-Nigh	t works	
g Wo Roa	d							
Drain	age and		ks at Nor	th side				
	Remo	val of Tei	mp Road	Reinsta	toment	of Planter	Area	
				itemste			Alca	
abondon	ed Lung I	King Stree	et					
	<u> </u>							
ge and U	tilities							
n/Road K	(erb							
nent Road			ns nt works					
		pavenie						
pply TTN								
Imp	lement T		nt Foot p	ath and C	entral Isl	and Cons	truction	
								Conventio

Page	2
------	---

ID	Task Name	Duration	Start	Finish		2021								2022										
					Dec	Jan	Feb Ma						Dec	Jan	Feb	Mar A	pr M	lay Ju	un 🗌	Jul	Aug	Sep	Oct	Nov De
181	Road Kerb and Footpath Pavement -South of Convention Avenue	48 d	Feb 3 '21	Mar 30 '21				Road Kerb and Footpath	Pavemen	t -South	of Conventi	on Avenue												
182	Middle Part- Remaining Drainage work	28 d	Jan 16 '21	Feb 17 '21			Middle	Part- Remaining Drainage wo	ĸ															
183	Middle Part- Irrigation works and Road Kerb	28 d	Feb 18 '21	Mar 22 '21				Middle Part- Irrigation wor	s and Ro	ad Kerb														
184	TTM2- Divert West direction to South	151 d	Jan 2 '21	Jun 28 '21																				
185	Apply TTM2 and Approval	75 d	Jan 2 '21	Mar 31 '21				Apply TTM2 and Approv	l															
186	Implement TTM2	12 d	Mar 31 '21	Apr 13 '21				Implement TTM2																
187	Remaining Drainage Works-Middle part	28 d	Apr 14 '21	May 17 '21				Remaining	Drainage	Works-N	/liddle part													
188	Irrigation and landscape works -Middle part	28 d	May 18 '21	Jun 18 '21					rigation a	nd lands	cape works	-Middle part												
189	Road Kerb-North of Comvention Anenue	18 d	Jun 8 '21	Jun 28 '21					Road Ke	rb-North	of Comven	tion Anenue												
190	TTM3- to Final Alignment	129 d	Apr 1 '21	Aug 31 '21																				
191	Apply TTM2 and Approval	75 d	Apr 1 '21	Jun 29 '21					Apply T	「M2 and	Approval													
192	Permanent TTM at PTI approval (no drawing now)	75 d	Apr 1 '21	Jun 29 '21					Perman	ent TTM	at PTI appro	oval (no drawii	ng now)											
193	Area C2-Road works Completed	0 d	Jun 29 '21	Jun 29 '21					Area C	-Road w	orks Comple	eted												
194	works at Expro East completed	0 d	Jun 29 '21	Jun 29 '21					works a	at Expro I	East comple	ted												
195	Implement TTM3- to Final Alignment	6 d	Jun 29 '21	Jul 6 '21					Imple	ment TTI	M3- to Final	Alignment												
196	Road Kerb and Footpath Pavement/road lighting -North of Convention	24 d	Jul 7 '21	Aug 3 '21						Road I	Kerb and Fo	otpath Pavem	ent/road	ighting -N	lorth of Co	nvention Av	enue							
197	Road Lighting /rails and Final touch up	24 d	Aug 4 '21	Aug 31 '21							Road Ligh	ting /rails and	Final tou	h up		Î								

	ιr	Iti	са	l

Critical Split

Task

Milestone •

Summary


**CEDD Entrusted Works** 

Critical

APPENDIX B

**Project Organization Structure** 

## Appendix B Project Organisation Structure

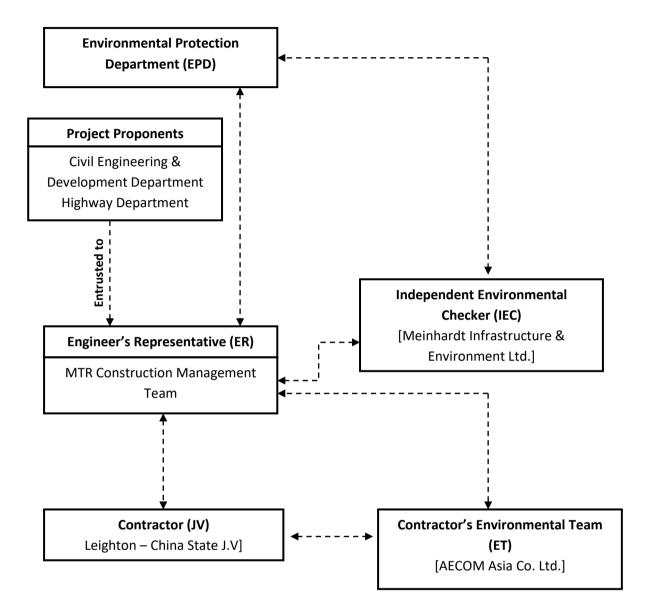

## APPENDIX C

Implementation Schedule of Environmental Mitigation Measures Leighton – China State J.V.

Appendix C – Environmental Mitigation Implementation Schedule

EIA Ref.	Recommended Mitigation Measures	Who to implement the measures?	Location of the measure
Construct	ion Dust Impact		
Construct	ion Phase		
S3.6.5	Four times a day watering of the work site with active operations	Contractor	Works areas
S3.8.1	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimise cumulative dust impacts.	Contractor	Works areas
	<ul> <li>Strictly limit the truck speed on site to below 10 km per hour and water spraying to keep the haul roads in wet condition;</li> </ul>		
	Watering during excavation and material handling;		
	<ul> <li>Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary; and</li> </ul>		
	Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.		
/	<ul> <li>Dust suppression measures (con't)</li> <li>De-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement</li> <li>The portion of any road where along the site boundary should be kept clear of dusty materials.</li> <li>Use of frequent watering for any dusty construction process (e.g. breaking works) to reduce dust emissions.</li> </ul>	Contractor	Works areas
/	<ul> <li>Emission from Vehicles and Plants</li> <li>All vehicles shall be shut down in intermittent use.</li> <li>Only well-maintained plant should be operated on-site and plant should be serviced regularly to avoid emission of black smoke.</li> <li>All diesel fuelled construction plant within the works areas shall be powered by ultra low sulphur diesel fuel (ULSD)</li> </ul>	Contractor	Works areas
Airborne I	Noise Impact		
Construct	ion Phase		
S4.9.4	<ul> <li>Good Site Practice:</li> <li>Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program.</li> <li>Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program.</li> <li>Mobile plant, if any, shall be sited as far away from NSRs as possible.</li> <li>Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum.</li> <li>Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.</li> <li>Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from onsite construction activities.</li> </ul>	Contractor	Works areas

## Shatin to Central Link 1123 - CEDD Entrusted Work Road P2 & other roads and Slip Road 3 Monthly EM&A Report for November 2021

When to implement the measures?	Implementation Status
Construction phase	V
Construction phase	
	@
	@
	V
	V
Construction phase	
	V V
	V
Construction phase	
	V
	V
	V
Construction phase	V
	V
	V V
	V
	V

Leighton – China State J.V.

## Appendix C – Environmental Mitigation Implementation Schedule

EIA Ref.	Recommended Mitigation Measures	Who to implement the measures?	Location of the measure	When to implement the measures?	Implementation Status
For DP1 –	CWB (Within the Project Boundary)				
S4.8.3 – S4.8.5	Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following tasks: <ul> <li>Slip road 8 tunnel</li> <li>Construction of diaphragm wall and substructures of the tunnel approach ramp</li> <li>Excavation</li> <li>Construction of slabs</li> <li>Backfill</li> <li>Demolition and construction of substructures for the IEC</li> <li>Demolition works of existing piers and crossheads of the marine section of the existing IEC</li> </ul>	Contractor	Works areas	Construction phase	N/A V V V N/A N/A N/A
	Use of PME grouping for the following tasks:				V
	At-grade roadwork				N/A
Tor DP2	Substructure for IECL connection  WDII Major Roads (Road P2)				
-01 DP2 - 64.8.3 -	Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following				
64.8.4	tasks:				
	Temporary road diversion				V
	Resurfacing				V
	At-grade roadwork				V
					V
Water Qua					V
	lity Impact				V
Constructi	lity Impact	Contractor	Works areas	Construction phase	
Constructi	Iity Impact         on Phase         Construction Runoff and Drainage:         • Use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of	Contractor	Works areas	Construction phase	V
Constructi	lity Impact         on Phase         Construction Runoff and Drainage:         • Use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;	Contractor	Works areas	Construction phase	V
Constructi	<ul> <li>lity Impact</li> <li>on Phase</li> <li>Construction Runoff and Drainage: <ul> <li>Use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;</li> <li>Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC</li> </ul> </li> </ul>	Contractor	Works areas	Construction phase	V V V
Constructi	<ul> <li>lity Impact</li> <li>on Phase</li> <li>Construction Runoff and Drainage: <ul> <li>Use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;</li> <li>Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94;</li> </ul> </li> </ul>	Contractor	Works areas	Construction phase	V V V V
Constructi	<ul> <li>Ity Impact</li> <li>on Phase</li> <li>Construction Runoff and Drainage: <ul> <li>Use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;</li> <li>Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94;</li> <li>A sediment tank constructed from preformed individual cells of approximately 6 - 8 m<sup>3</sup> capacity can be used for</li> </ul> </li> </ul>	Contractor	Works areas	Construction phase	V V V V
Constructi	<ul> <li>Ity Impact</li> <li>Ity Impact</li> <li>on Phase</li> <li>Construction Runoff and Drainage: <ul> <li>Use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;</li> <li>Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94;</li> <li>A sediment tank constructed from preformed individual cells of approximately 6 - 8 m<sup>3</sup> capacity can be used for settling ground water prior to disposal;</li> <li>Oil interceptors shall be provided in the drainage system for the tunnels and regularly cleaned to prevent the</li> </ul> </li> </ul>	Contractor	Works areas	Construction phase	V V V V V
Constructi	<ul> <li>Ity Impact</li> <li>on Phase</li> <li>Construction Runoff and Drainage: <ul> <li>Use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;</li> <li>Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94;</li> <li>A sediment tank constructed from preformed individual cells of approximately 6 - 8 m<sup>3</sup> capacity can be used for settling ground water prior to disposal;</li> <li>Oil interceptors shall be provided in the drainage system for the tunnels and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor shall have a bypass to prevent flushing during periods of heavy rain;</li> </ul> </li> </ul>	Contractor	Works areas	Construction phase	V V V V V V
Constructi	<ul> <li>Ity Impact</li> <li>on Phase</li> <li>Construction Runoff and Drainage: <ul> <li>Use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;</li> <li>Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94;</li> <li>A sediment tank constructed from preformed individual cells of approximately 6 - 8 m<sup>3</sup> capacity can be used for settling ground water prior to disposal;</li> <li>Oil interceptors shall be provided in the drainage system for the tunnels and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor shall</li> </ul> </li> </ul>	Contractor	Works areas	Construction phase	V V V V V V V
Constructi	<ul> <li>Iity Impact</li> <li>on Phase</li> <li>Construction Runoff and Drainage: <ul> <li>Use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;</li> <li>Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94;</li> <li>A sediment tank constructed from preformed individual cells of approximately 6 - 8 m<sup>3</sup> capacity can be used for settling ground water prior to disposal;</li> <li>Oil interceptors shall be provided in the drainage system for the tunnels and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor shall have a bypass to prevent flushing during periods of heavy rain;</li> <li>Precautions and actions to be taken when a rainstorm is imminent or forecast, and during or after rainstorms. Particular attention shall be paid to the control of any silty surface runoff during storm events;</li> <li>On-site drainage system shall be installed prior to the commencement of other construction activities. Sediment</li> </ul> </li> </ul>	Contractor	Works areas	Construction phase	
Water Qua Construction S5.8	<ul> <li>Iity Impact</li> <li>on Phase</li> <li>Construction Runoff and Drainage: <ul> <li>Use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;</li> <li>Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94;</li> <li>A sediment tank constructed from preformed individual cells of approximately 6 - 8 m<sup>3</sup> capacity can be used for settling ground water prior to disposal;</li> <li>Oil interceptors shall be provided in the drainage system for the tunnels and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor shall have a bypass to prevent flushing during periods of heavy rain;</li> <li>Precautions and actions to be taken when a rainstorm is imminent or forecast, and during or after rainstorms. Particular attention shall be paid to the control of any silty surface runoff during storm events;</li> </ul> </li> </ul>		Works areas	Construction phase	V V V V V V V V

## Shatin to Central Link 1123 - CEDD Entrusted Work Road P2 & other roads and Slip Road 3 Monthly EM&A Report for November 2021

AECOM

Appendix C – Environmental Mitigation Implementation Schedule

EIA Ref.	Recommended Mitigation Measures	Who to implement the measures?	Location of the measure
	Minimum distances of 100 m shall be maintained between the storm water discharges and the existing or planned WSD flushing water intakes during construction phase		
S5.8	Sewage from Construction Work Force: Construction work force sewage discharges on site shall be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage shall be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor shall also be responsible for waste disposal and maintenance practices.	Contractor	Works areas
S5.8	<i>Floating Debris and Refuse:</i> Collection and removal of floating refuse shall be performed at regular intervals on a daily basis. The contractor shall be responsible for keeping the water within the site boundary and the neighbouring water free from rubbish.	Contractor	Works areas and adjacent water
S5.8	Storm Water Discharges: Minimum distances of 100 m shall be maintained between the existing or planned stormwater discharges and the existing or planned WSD flushing water intakes.	Contractor	Works areas and adjacent water
Waste Ma	nagement Implications	I	
Construct	tion Phase		
S6.7.7	<ul> <li>Good Site Practices:</li> <li>Recommendations for good site practices during the construction activities include:</li> <li>Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site;</li> <li>Training of site personnel in proper waste management and chemical waste handling procedures;</li> <li>Provision of sufficient waste disposal points and regular collection for disposal;</li> <li>Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;</li> <li>Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and</li> <li>A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).</li> </ul>	Contractor	Works areas
S6.7.8	<ul> <li>Waste Reduction Measures:</li> <li>Recommendations to achieve waste reduction include:</li> <li>Sort C&amp;D waste from demolition of the existing waterfront structures to recover recyclable portions such as metals.</li> <li>Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.</li> <li>Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force.</li> <li>Any unused chemicals or those with remaining functional capacity shall be recycled.</li> <li>Use of reusable non-timber formwork, such as in casting the tunnel box sections, to reduce the amount of C&amp;D material.</li> <li>Prior to disposal of C&amp;D waste, it is recommended that wood, steel and other metals shall be separated for reuse and / or recycling to minimise the quantity of waste to be disposed of to landfill.</li> <li>Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> <li>Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.</li> </ul>	Contractor	Works areas

# Shatin to Central Link 1123 - CEDD Entrusted Work Road P2 & other roads and Slip Road 3 Monthly EM&A Report for November 2021

When to implement the measures?	Implementation Status
	V
Construction phase	V
Construction phase	V
Construction phase	V
During planning and design stage, and construction stage	V
	V V V
	V V
During planning and design stage, and construction stage	V
Slage	V
	V
	V V
	V
	V
	V

# Appendix C – Environmental Mitigation Implementation Schedule

EIA Ref.	Recommended Mitigation Measures	Who to implement the measures?	Location of the measure	When to implement the measures?	Implementation Status
S6.7.10	General Refuse:     General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A licensed	Contractor	Works areas	Construction phase	V
	<ul> <li>waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&amp;D material.</li> <li>A collection area shall be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind blow' light material.</li> </ul>				@
\$6.7.11	<i>Chemical Wastes:</i> After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals shall be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Contractor	Works areas	Construction phase	V
S6.7.12 – S6.7.13	<ul> <li>Construction and Demolition Material:</li> <li>C&amp;D material shall be sorted on-site into inert C&amp;D material (that is, public fill) and C&amp;D waste. All the suitable inert C&amp;D material shall be broken down to 250 mm in size for reuse as public fill in the WDII reclamation. C&amp;D waste, such as wood, glass, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials.</li> <li>In order to monitor the disposal of public fill and C&amp;D waste at public fill reception facilities and landfills, respectively, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team undertaking the environmental monitoring and audit work. An Independent Environment Checker shall be responsible for auditing the results of the system.</li> </ul>	Contractor	Works areas	Construction phase	V V
6.7.14	<ul> <li>Bentonite Slurry: The disposal of residual used bentonite slurry shall follow the good practice guidelines stated in ProPECC PN 1/94 "Construction Site Drainage" and listed as follows:</li> <li>If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis.</li> <li>If the used bentonite slurry is intended to be disposed of through the public drainage system, it shall be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the Technical Memorandum of Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters.</li> <li>If the used bentonite slurry is intended to be disposed to public fill reception facilities, it will be mixed with dry soil on site before disposal.</li> </ul>	Contractor	Works areas	Construction phase	N/A N/A N/A
/	<ul> <li>Soli on site before disposal.</li> <li>Accidental spillage To prevent accidental spillage of chemicals, the following is recommended: <ul> <li>Proper storage and handling facilities will be provided.</li> <li>All the tanks, containers, storage area will be bunded and the locations will be locked as far as possible from the sensitive watercourse and stormwater drains. <li>The contractor will register as a chemical waste producer if chemical wastes would be generated. Storage of chemical waste arising from the construction activities will be stored with suitable labels and warnings.</li> <li>Disposal of chemical wastes will be conducted in compliance with the requirements as stated in the Waste disposal (Chemical Waste) (General) Regulation.</li> </li></ul></li></ul>	Contractor	Works areas	Construction phase	V V V V
Land Cont	amination Impact				
S.7.1.1	As no potential contaminative land uses were identified within the Study Area, adverse land contamination impacts associated with the construction and operation of the Project is not expected. As such, environmental protection and mitigation measures are considered not necessary and will not be covered in this EM&A Manual.	-	-	-	N/A

# Shatin to Central Link 1123 - CEDD Entrusted Work Road P2 & other roads and Slip Road 3 Monthly EM&A Report for November 2021

Leighton – China State J.V.

Appendix C – Environmental Mitigation Implementation Schedule

EIA Ref.	Recommended Mitigation Measures	Who to implement the measures?	Location of the measure	
Landscape	and Visual			
Construct	ion Phase			
For DP1 -	CWB (Within the Project Boundary) and DP2 - WDII Major Roads (Road P2)			
Table 10.5	<ul> <li>CM1 - Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.</li> <li>CM2 - Existing trees to be retained on site shall be carefully protected during construction.</li> <li>CM3 - Trees unavoidably affected by the works shall be transplanted where practical.</li> <li>CM4 - Compensatory tree planting shall be provided to compensate for felled trees.</li> <li>CM5 - Control of night-time lighting.</li> <li>CM6 - Erection of decorative screen hoarding compatible with the surrounding setting.</li> </ul>	Contractor	Works areas	

Legend: V = implemented;

= not implemented; Х

@ = partially implemented;

N/A = not applicable

# Shatin to Central Link 1123 - CEDD Entrusted Work Road P2 & other roads and Slip Road 3 Monthly EM&A Report for November 2021

When to implement the measures?	Implementation Status
Construction phase	V
	N/A
	N/A
	N/A
	V
	N/A

APPENDIX D

Summary of Action and Limit Levels

# Appendix D – Summary of Action and Limit Levels

Table 1 Action and Limit Levels for 24-hou	' TSP
--	-------

ID	Location Action Level		Limit Level
CMA5b	Pedestrian Plaza	209.9 μg/m³	260 μg/m³
CMA6a	WDII PRE Site Office	207.1 μg/m <sup>3</sup>	260 μg/m³

# Table 2 Action and Limit Levels for 1-hour TSP

ID	Location Action Level		Limit Level	
CMA5b	Pedestrian Plaza	339.7 μg/m³	500 μg/m³	
CMA6a	WDII PRE Site Office	333 μg/m³	500 μg/m³	

# Table 3Action and Limit Levels for Construction Noise(0700 – 1900 hrs of normal weekdays)

ID	Location	Action Level	Limit Level
M1a	Footbridge at EX-Wanchai Harbour Road Sports Centre	When one documented complaint is received	75 dB(A)

APPENDIX E

**Calibration Certificates of Equipments** 

TIC	36							ALIBRATION DUE DATE:
							Janu	Jary 7, 2022
Envir	onm	ent	al					
	C1	2	çate g	/			rtion	
			Calibration	Certificati	on Information	tion		
Cal. Date:	January 7,	2021	Rootsr	meter S/N:	438320	Ta:	294	°K
Operator:	Jim Tisch					Pa:	756.4	mm Hg
Calibration	Model #:	TE-5025A	Calib	prator S/N:	0843			
		Vol. Init	Vol. Final	ΔVol.	∆Time	ΔP	ΔН	]
	Run	(m3)	(m3)	(m3)	(min)	(mm Hg)	(in H2O)	
	1	1	2	1	1.3970	4.2	2.00	
	2	3	4	1	0.9930	6.4	4.00	
	4	7	8	1	0.8420	8.0	5.00	-
	5	9	10	1	0.6950	12.7	8.00	-
			D	ata Tabula	tion			]
				V Total				
	Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right)}$	$-)(-\frac{1510}{Ta})$		Qa	√∆Н(Та/Ра)	
	(m3)	(x-axis)	(y-axi		Va	(x-axis)	(y-axis)	
	1.0032	0.7181	1.420		0.9944	0.7118	0.8817	
	1.0003 0.9982	1.0073	2.008		0.9915	0.9985	1.2469	
	0.9972	1.1330	2.245		0.9894	1.1256	1.3941	
	0.9919	1.4272	2.840		0.9832	1.4147	1.4621	
		m=	1.999	14		m=	1.25183	
	QSTD	b=	-0.013		QA	b=	-0.00854	
		r=	0.999	91		r=	0.99991	
				Calculation	ıs	1		
			/Pstd)(Tstd/Ta	)		∆Vol((Pa-∆l	P)/Pa)	
	Qstd=	Vstd/∆Time			and the second se	Va/∆Time		
		//	For subseque	ent flow rat	te calculation	ns:		
	Qstd=	1/m (( \\ \ \ \ \ \ \ H (	$\frac{Pa}{Pstd}$ $\left(\frac{Tstd}{Ta}\right)$	)-ь)	Qa=	1/m ((√∆H	l(Та/Ра))-b)	
		Conditions	1					
Tstd:							IBRATION	
Pstd:	Pstd: 760 mm Hg Key US EPA recommends annual r						nual recalibratio	n nor 1008
ΔH: calibrato			n H2O)				legulations Part 5	
ΔP: rootsme	ter manome	eter reading					Reference Meth	
Ta: actual ab							ended Particulate	
Pa: actual ba b: intercept	rometric pr	essure (mm	Hg)				re, 9.2.17, page 3	
m: slope				L				
Long and the second sec					414			

Tisch Environmental, Inc.

145 South Miami Avenue

Village of Cleves, OH 45002

<u>www.tisch-env.com</u> TOLL FREE: (877)263-7610 FAX: (513)467-9009

# AECOM Asia Company Limited <u>TSP High Volume Sampler</u> <u>Field Calibration Report</u>

WDII PRE Site Of	îce	Operator:	Shum Kam Yuen	_
15 Sep 2021		Next Due Date:	15 Nov 2021	
A-001-79T		Serial No.	3384	_
		Ambient Condition		
re, Ta (K)	303.0	Pressure, Pa (mmHg)	757.2	
		Orifice Transfer Standard Information		
	15 Sep 2021 A-001-79T	A-001-79T	15 Sep 2021         Next Due Date:           A-001-79T         Serial No.           Ambient Condition	Mbit Hit2 Gite Gited         Openation         Image: Constraint of the constra

Orifice Transfer Standard Information								
Serial No:	843	Slope, mc	1.99914	Intercept, bc	-0.1375			
Last Calibration Date: 7 Jan 2021 $mc x Qstd + bc = [DH x (Pa/760) x (298/Ta)]^{1/2}$								
Next Calibration Date:	7 Jan 2022	Qstd = {[DH x (Pa/760) x (298/Ta)] <sup>1/2</sup> -bc} / mc						

			of TSP Sampler		
		Orfice		HVS	S Flow Recorder
Resistance Plate No.	DH (orifice)		Qstd (m <sup>3</sup> /min) X - axis	Flow Recorder Reading (CFM)	Continuous Flow Recorder Reading IC (CFM) Y-axis
18	7.0	2.62	1.38	45.0	44.54
13	6.0	2.42	1.28	40.0	39.60
10	4.5	2.10	1.12	33.0	32.67
7	3.1	1.74	0.94	24.0	23.76
5	2.4	1.53	0.84	20.0	19.80
Slope , mw = Correlation Coe		0.9987	Intercept, bw =	-18.	8437
Slope , mw = Correlation Coe	45.8197 efficient* =		Intercept, bw =	-18.	8437
Slope , mw = Correlation Coe	45.8197 efficient* =	check and recalibrate.	Intercept, bw =	-18,4	8437
Slope , mw = Correlation Coe *If Correlation Co	45.8197 efficient* = 	check and recalibrate.	_	-18.	8437
Slope , mw = Correlation Coe *If Correlation Co From the TSP F	45.8197 efficient* = pefficient < 0.990, of ield Calibration Cur	check and recalibrate. Set Point	_	-18.	8437
Slope , mw = Correlation Coe *If Correlation Co From the TSP F	45.8197 efficient* = pefficient < 0.990, of ield Calibration Cur	check and recalibrate. Set Point rve, take Qstd = 1.30m <sup>3</sup> /min	Calculation		8437
Slope , mw = Correlation Coe *If Correlation Coe From the TSP F From the Regres	45.8197 efficient* = cefficient < 0.990, of field Calibration Cur assion Equation, the	check and recalibrate. Set Point rve, take Qstd = 1.30m <sup>3</sup> /min "Y" value according to	x [(Pa/760) x (298/		41.14

QC Reviewer: US CHIKN

Signature: \_

R

Date: 15/9/21

C:\Old data\HVS Calibration Certificate (Existing)\60436763

# AECOM Asia Company Limited <u>TSP High Volume Sampler</u> <u>Field Calibration Report</u>

Station	WDII PRE Site Of	fice	Operator:	Shum Kam Yuen	
Cal. Date:	15 Nov 2021		Next Due Date:	15 Jan 2022	
Equipment No.:	A-001-79T	-	Serial No.	3384	•
			Ambient Condition		
Temperat	ure, Ta (K)	298.0	Pressure, Pa (mmHg)	761.6	

	(	Drifice Transfer St	andard Information		
Serial No:	843	Slope, mc	1.99914	Intercept, bc	-0.1375
Last Calibration Date:	7 Jan 2021		mc x Qstd + bc = [[	DH x (Pa/760) x (298/Ta)] <sup>1/2</sup>	
Next Calibration Date:	7 Jan 2022		Qstd = {[DH x (Pa/)	760) x (298/Ta)] <sup>1/2</sup> -bc} / mc	

		Calibration of	of TSP Sampler		
		Orfice		HVS	S Flow Recorder
Resistance Plate No.	DH (orifice), in. of water	[DH x (Pa/760) x (298/Ta)] <sup>1/2</sup>	Qstd (m <sup>3</sup> /min) X · axis	Flow Recorder Reading (CFM)	Continuous Flow Recorder Reading IC (CFM) Y-axis
18	6.9	2.63	1.38	45.0	45.05
13	5.9	2.43	1.29	40.0	40.04
10	4.5	2.12	1.13	34.0	34.04
7	3.0	1.73	0.94	25.0	25.03
5	2.4	1.55	0.84	20.0	20.02
*If Correlation C	oefficient < 0.990,	check and recalibrate.			
			Calculation		
		rve, take Qstd = 1.30m <sup>3</sup> /min			
From the Regre	ssion Equation, the	e "Y" value according to			
		mw x Qstd + bw = IC	x [(Pa/760) x (298/	Ta)] <sup>1/2</sup>	
Therefore, Set F	Point; IC = ( mw x C	Qstd + bw ) x [( 760 / Pa ) x ( Ta / 2	98 )] <sup>1/2</sup> =		41.14
Remarks:					
Remarks:					

C:\Old data\HVS Calibration Certificate (Existing)\60436763

# AECOM Asia Company Limited <u>TSP High Volume Sampler</u> <u>Field Calibration Report</u>

Station	Pedestrian Plaza	<i>´</i>		Operator:	Choi W	/ing Ho	
Cal. Date:	15-Oct-21			Next Due Date:	15-De	ec-21	•
Equipment No.:	A-001-70T			Serial No.	10273		-
			Ambient C	ondition			
Temperat	ture, Ta (K)	300	Pressure, Pa	(mmHg)		756.6	
					10 / - Kere		
			Orifice Transfer Star	ndard Information			
Seri	al No:	843	Slope mc	1 99914		Intercent bc	-0.01375

mc x Qstd + bc =  $[H x (Pa/760) x (298/Ta)]^{1/2}$ 

		Calibration of	of TSP Sampler			
		Orfice		HVS Flow Recorder		
Resistance Plate No. in. of water	[DH x (Pa/760) x (298/Ta)] <sup>1/2</sup>	Qstd (m <sup>3</sup> /min) X · axis	Flow Recorder Reading (CFM)	Continuous Flow Recorder Reading IC (CFM) Y-axis		
18	6.8	2.59	1.30	44.0	43.75	
13	5.6	2.35	1.18	38.0	37.79	
10	4.6	2.13	1.07	33.0	32.82	
7	3.5	1.86	0.94	26.0	25.86	
5	2.6	1.60	0.81	20.0	19.89	
	ession of Y on X 48.2634		Intercept, bw =	-19.2	2178	
Slope , mw =	8					
	efficient* =	0.9997		14 Act 45 1		
Correlation Coe		0.9997	-		÷	

From the Regression Equation, the "Y" value according to

Last Calibration Date:

Next Calibration Date:

# mw x Qstd + bw = IC x [(Pa/760) x (298/Ta)]<sup>1/2</sup>

Therefore, Set Point; IC = ( mw x Qstd + bw ) x [( 760 / Pa ) x ( Ta / 298 )]<sup>1/2</sup>=

07-Jan-21

07-Jan-22

Remarks:						
QC Reviewer:	WS	CHAN	Signature:	R	Da	le: <u>15/10/21</u>

C:\Old data\HVS Calibration Certificate (Existing

43.77

# EQUIPMENT CALIBRATION RECORD

Model No Equipmen Sensitivity	t No.:	Laser Dust Monitor         nd:       SIBATA         LD-3         A.005.09a         nent Scale Setting:       797 CPM         Mike Shek (MSKM)				-	
Operator:			Mike She	k (MSKM)			-
Standard I	Equimment						
	: ation Date:	ũ			ler It Secondary Scho	ol	-
Calibration	n Result						
	Adjustment Sca Adjustment Sca					797 797	СРМ
Hour	Date	Time	Ambient	Condition	Concentration (1)	Total Count (2)	Count/
	(dd/mm/yy)		Temp (°C)	R.H.(%)	(mg/m3)		Minute ③
					Y-axis		X-axis
1	30/04/21	9:30-10:30	28.0	78	0.04950	1980	33.00
2	30/04/21	10:30-11:30	28.0	78	0.05045	2030	33.83
3	30/04/21	11:30-12:30	28.0	78	0.05250	2120	35.33
Note:		12:30-13:30 data was measu was logged by L te was calculate	aser Dust I	Monitor	an a	2310	38.50
By Linear F	Regression of Y o	n X					
	Slope (K-factor)	:	0.0015				
	Correlation coef	ficient:	0.9997				
Validity of	Calibration Reco	ord:	30-Aj	or-22			
Remarks:							

QC Reviewer: YWFmg Signature: Date: 3-May 21

# **EQUIPMENT CALIBRATION RECORD**

Type:			Laser Dus	st Monito	r		
Manufact	urer/Brand:		SIBATA				-
Model No	.:		LD-3				-
Equipmen	t No.:		A.005.10	а			-
Sensitivity	Adjustment Sca	le Setting:	753 CPM				_
Operator:			Mike She	k (MSKM)			-
							-
Standard I	Equimment						
Equipmen	t:		High Volu	ime Samp	ler		_
Venue:			Fanling G	overnmer	nt Secondary Scho	ol	
Model No	.:		TE-5170				-
Serial No.:			3154				
Last Calibr	ation Date:		23-Apr-22	1			
Calibration	n Result		1				
	Adjustment Sca					753	СРМ
Sensitivity	Adjustment Sca	le Setting (After	Calibratio	n):		753	СРМ
r							
Hour	Date	Time	Ambient	Condition	Concentration	Total Count (2)	Count/
	(dd/mm/yy)		Temp (°C)	R.H.(%)	(mg/m3)		Minute(3)

	(dd/mm/yy)		Temp (°C)	R.H.(%)	(mg/m3)		Minute ③
					Y-axis		X-axis
1	30/04/21	9:30-10:30	28.0	78	0.04950	1945	32.42
2	30/04/21	10:30-11:30	28.0	78	0.05045	2010	33.50
3	30/04/21	11:30-12:30	28.0	78	0.05250	2110	35.17
4	30/04/21	12:30-13:30	28.0	78	0.05520	2310	38.50
Note:	(1) Monitoring	data was measu	red by Hig	h Volume	Sampler		

1 Monitoring data was measured by High Volume Sampler

(2) Total Count was logged by Laser Dust Monitor

③ Count/minute was calculated by (Total Count/60)

By Linear Regression of Y on X	
Slope (K-factor):	0.0015
Correlation coefficient:	0.9994
Validity of Calibration Record:	30-Apr-22

Remarks:

QC Reviewer:

Yuring Signature: Y Date: 3-May-21





# **CERTIFICATE OF CALIBRATION**

21CA0309 02			Page	1 of 2	
	(Type 1)	,	Microphone	Pream	
		,			
		,			
2644597		,	2879980	29398	
-		,	-	-	
AECOM ASIA CO	LTD				
-					
-					
09-Mar-2021					
22-Mar-2021					
used in the calibr	ation				
Model:	Serial No.		Expiry Date:	Traceable to:	
B&K 4226	2288444		23-Aug-2021	CIGISMEC	
DS 360	33873		19-May-2021	CEPREI	
22 ± 1 °C					
55 ± 10 %					
	B & K 2270 2644597 - AECOM ASIA CO - - 09-Mar-2021 22-Mar-2021 used in the calibr Model: B&K 4226	2270 2644597 - AECOM ASIA CO LTD - - 09-Mar-2021 22-Mar-2021 <b>used in the calibration</b> <b>Model: Serial No.</b> B&K 4226 2288444	B & K 2270 2644597 - AECOM ASIA CO LTD - 09-Mar-2021 22-Mar-2021 used in the calibration Model: Serial No. B&K 4226 2288444	B & K 2270 , 4950 2644597 , 2879980 	B & K       B & K       B & K         2270       4950       ZC0032         2644597       2879980       29398         -       -       -         AECOM ASIA CO LTD       -       -         -       -       -         09-Mar-2021       -       -         used in the calibration       Expiry Date:       Traceable to:         B&K 4226       2288444       23-Aug-2021       CIGISMEC

- 1, The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- 2. The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of <u>+</u>20%.
- The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

#### **Test results**

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Approved Signatory:

Feng Jungi

24-Mar-2021 Company Chop:



**Comments:** The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument. The results apply to the item as received.

Date:

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-1/Issue 1/Rev.C/01/02/2007



SUILS & MATERIALS ENGINEERING CO., LTD. 香港新界葵涌永基路22-24號好爸爸創科大廈

Good Ba Ba Hitech Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com



2

# CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

21CA0309 02

2 of

Page

#### 1, Electrical Tests

The electrical tests were perfomed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Uncertanity (dB) / Coverage Factor
Self-generated noise	А	Pass	0.3
	С	Pass	1.0 2.1
	Lin	Pass	2.0 2.2
Linearity range for Leq	At reference range, Step 5 dB at 4 kHz	Pass	0.3
	Reference SPL on all other ranges	Pass	0.3
	2 dB below upper limit of each range	Pass	0.3
	2 dB above lower limit of each range	Pass	0.3
Linearity range for SPL	At reference range , Step 5 dB at 4 kHz	Pass	0.3
Frequency weightings	A	Pass	0.3
	С	Pass	0.3
	Lin	Pass	0.3
Time weightings	Single Burst Fast	Pass	0.3
	Single Burst Slow	Pass	0.3
Peak response	Single 100µs rectangular pulse	Pass	0.3
R.M.S. accuracy	Crest factor of 3	Pass	0.3
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3
	Repeated at frequency of 100 Hz	Pass	0.3
Time averaging	1 ms burst duty factor 1/10 <sup>3</sup> at 4kHz	Pass	0.3
	1 ms burst duty factor 1/10 <sup>4</sup> at 4kHz	Pass	0.3
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4
Overload indication	SPL	Pass	0.3
	Leq	Pass	0.4

#### 2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Uncertanity (dB) / Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3
	Weighting A at 8000 Hz	Pass	0.5

#### 3, Response to associated sound calibrator

N/A

The uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95 %. A coverage factor of 2 is assumed unless explicitly stated.

End Calibrated by: Checked by Fung Chi Yip Chan Yuk Yiu Date: 22-Mar-2021 Date: 24-Mar-2021

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-2/Issue 1/Rev.C/01/02/2007



香港新界葵涌永基路22-24號好爸爸創科大廈 Good Ba Ba Hitech Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com



# **CERTIFICATE OF CALIBRATION**

Certificate No.:	21CA0319 01-01		Page	1	of	2
Item tested						
Description:	Sound Level Mete	er (Type 1)	Microphone		Preamp	
Manufacturer:	B & K		B&K		B&K	
Type/Model No.:	2250-L		4950		ZC0032	
Serial/Equipment No.:	2681366		2665582		17190	
Adaptors used:	-		-		-	
Item submitted by						
Customer Name:	AECOM ASIA CO	LTD				
Address of Customer:	-					
Request No.:	-					
Date of receipt:	19-Mar-2021					
Date of test:	23-Mar-2021					
		ration				
Reference equipment		ration Serial No.	Expiry Date:		Traceabl	e to:
Reference equipment	used in the calib		Expiry Date: 23-Aug-2021		Traceabl	
Reference equipment Description: Multi function sound calibrator	used in the calib Model:	Serial No.	<b>Expiry Date:</b> 23-Aug-2021 19-May-2021		Traceabl CIGISMEC CEPREI	
Date of test: Reference equipment Description: Multi function sound calibrator Signal generator Ambient conditions	used in the calib Model: B&K 4226	Serial No. 2288444	23-Aug-2021		CIGISMEC	
Reference equipment Description: Multi function sound calibrator Signal generator	used in the calib Model: B&K 4226	Serial No. 2288444	23-Aug-2021		CIGISMEC	
Reference equipment Description: Multi function sound calibrator Signal generator Ambient conditions	used in the calib Model: B&K 4226 DS 360	Serial No. 2288444	23-Aug-2021		CIGISMEC	

- 1, The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- 2, The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.
- 3. The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

#### **Test results**

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Approved Signatory:

U Feng Jungi

24-Mar-2021 Company Chop:



**Comments:** The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument. The results apply to the item as received.

Date:

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-1/Issue 1/Rev.C/01/02/2007



香港新界葵涌永基路22-24號好爸爸創科大廈 Good Ba Ba Hitech Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com



# **CERTIFICATE OF CALIBRATION**

(Continuation Page)

Certificate No.:

21CA0319 01-01

2 of

Page

2

#### 1, Electrical Tests

The electrical tests were perfomed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
		otatuo.	oncertainty (ub)	1 actor
Self-generated noise	A	Pass	0.3	
	С	Pass	0.8	
	Lin	Pass	1.6	
Linearity range for Leq	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	A	Pass	0.3	
	С	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	Pass	0.3	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/10 <sup>3</sup> at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 <sup>4</sup> at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

#### 2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
	Weighting A at 8000 Hz	Pass	0.5	

#### 3, Response to associated sound calibrator

#### N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.



The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-2/Issue 1/Rev.C/01/02/2007



# 綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香港新界葵涌永基路 2 2 - 2 4 號好爸爸創科大廈

Good Ba Ba Hitech Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com



# **CERTIFICATE OF CALIBRATION**

Certificate No.:	21CA0319 01-02	2	Page:	1	of	2
Item tested						
Description:	Acoustical Calib	rator (Class 1)				
Manufacturer:	MVI					
Type/Model No.:	CAL21					
Serial/Equipment No.:	34113610(2011)	/ N.004.11				
Adaptors used:	Yes (BAC21)					
Item submitted by						
Curstomer:	AECOM ASIA C	O., LTD.				
Address of Customer:	-	62.5				
Request No.:	-					
Date of receipt:	19-Mar-2021					
Date of test:	23-Mar-2021					
Reference equipment	used in the cali	bration				
Description:	Model:	Serial No.	Expiry Date:	e	Traceabl	e to:
Lab standard microphone	B&K 4180	2412857	11-May-2021		SCL	
Preamplifier	B&K 2673	2743150	03-Jun-2021		CEPREI	
Measuring amplifier	B&K 2610	2346941	03-Jun-2021	)	CEPREI	
Signal generator	DS 360	33873	19-May-2021		CEPREI	
Digital multi-meter	34401A	US36087050	19-May-2021		CEPREI	
Audio analyzer	8903B	GB41300350	18-May-2021		CEPREI	
Universal counter	53132A	MY40003662	18-May-2021		CEPREI	
Ambient conditions						
Temperature:	22 ± 1 °C					
Relative humidity:	55 ± 10 %					

#### **Test specifications**

Air pressure:

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- 2, The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- 3. The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

#### **Test results**

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.

1005 ± 5 hPa

Approved Signatory:

Feng Junqi

24-Mar-2021 Company Chop:



Comments: The results reported in this certificate refer to the conditon of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument. The results apply to the item as received.

Date:

© Soils & Materials Engineering Co., Ltd.

Form No.CARP156-1/Issue 1/Rev.D/01/03/2007



香港新界葵涌永基路22-24號好爸爸創科大廈 Good Ba Ba Hitech Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com



# **CERTIFICATE OF CALIBRATION**

(Continuation Page)

Certificate No.:

1,

21CA0319 01-02

Page: 2 of 2

Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

Frequency	Output Sound Pressure	Measured Output	Estimated Expanded
Shown	Level Setting	Sound Pressure Level	Uncertainty
Hz	dB	dB	dB
1000	94.00	93.98	0.10

#### 2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz	STF = 0.010 dB
Estimated expanded uncertainty	0.005 dB

#### 3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz	Actual Frequency = 1002.6 Hz	
Estimated expanded uncertainty	0.1 Hz	Coverage factor k = 2.2

#### 4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz	TND = 1.8 %
Estimated expanded uncertainty	0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

	Λ	- End -	
Calibrated by:	1~1	Checked by:	Jack
	Fung Chi Yip		Chan Yuk Yiu
Date:	23-Mar-2021	Date:	24-Mar-2021

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co., Ltd.

Form No.CARP156-2/Issue 1/Rev.C/01/05/2005



香港新界葵涌永基路22-24號好爸爸創科大廈 Good Ba Ba Hitech Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com



# CERTIFICATE OF CALIBRATION

Certificate No.:	21CA0401 02		Page:	1	of	2
Item tested						
Description:	Acoustical Calibra	ator (Class 1)				
Manufacturer:	B & K					
Type/Model No.:	4231					
Serial/Equipment No .:	3006428					
Adaptors used:						
Item submitted by						
Curstomer:	AECOM					
Address of Customer:	-					
Request No.:	-					
Date of receipt:	01-Apr-2021					
Date of test:	05-Apr-2021					
Reference equipment	used in the calil	oration				
Description:	Model:	Serial No.	Expiry Date:		Traceable	to:
Lab standard microphone	B&K 4180	2412857	11-May-2021		SCL	
Preamplifier	B&K 2673	2743150	03-Jun-2021		CEPREI	
Measuring amplifier	B&K 2610	2346941	03-Jun-2021		CEPREI	

Signal generator	DS 360	33873	19-May-2021
Digital multi-meter	34401A	US36087050	19-May-2021
Audio analyzer	8903B	GB41300350	18-May-2021
Universal counter	53132A	MY40003662	18-May-2021
A			

#### Ambient conditions

Temperature:	22 ± 1 °C
Relative humidity:	55 ± 10 %
Air pressure:	1010 ± 5 hPa

#### **Test specifications**

- 1, The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- 2. The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference 3, pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

#### Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.

Feng Junqi

07-Apr-2021 Company Chop:



Comments: The results reported in this certificate refer to the conditon of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument. The results apply to the item as received.

Date:

© Soils & Materials Engineering Co., Ltd

**Approved Signatory:** 

Form No.CARP156-1/Issue 1/Rev.D/01/03/2007

CEPREI

CEPREI

CEPREI

CEPREI



香港新界葵涌永基路22-24號好爸爸創科大廈 Good Ba Ba Hitech Building, Nos. 22-24 Wing Kei Road, Kwai Chung, New Territories, Hong Kong Tel: (852) 2873 6860 Fax: (852) 2555 7533 E-mail: smec@cigismec.com Website: www.cigismec.com



2

# CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

21CA0401 02

Page: 2 of

#### 1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

Frequency	Output Sound Pressure	Measured Output	Estimated Expanded
Shown	Level Setting	Sound Pressure Level	Uncertainty
Hz	dB	dB	dB
1000	94.00	94.23	0.10

#### 2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz	STF = 0.016 dB
Estimated expanded uncertainty	0.005 dB

#### 3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz	Actual Frequency = 999.95 Hz	
Estimated expanded uncertainty	0.1 Hz	Coverage factor k = 2.2

#### 4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz	TND = 0.3 %
Estimated expanded uncertainty	0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

	1	- End -	$\sim$ 1
Calibrated by:	1	Checked by:	Jack
	Fung Chi Yip		Chan Yuk Yiu
Date:	05-Apr-2021	Date:	07-Apr-2021

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co., Ltd.

APPENDIX F

EM&A Monitoring Schedules

### Shatin to Central Link 1123 - CEDD Entrusted Work Road P2 & other roads and Slip Road 3 **Tentative Impact Monitoring Schedule for November 2021**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Nov	2-Nov	3-Nov	4-Nov	5-Nov	6-Nov
	1-hour TSP	Noise			24-hour TSP	1-hour TSP
7-Nov	8-Nov	9-Nov	10-Nov	11-Nov	12-Nov	13-Nov
				24-hour TSP Noise	1-hour TSP	
14-Nov	15-Nov	16-Nov	17-Nov	18-Nov	19-Nov	20-Nov
			24-hour TSP Noise	1-hour TSP		
21-Nov	22-Nov	23-Nov	24-Nov	25-Nov	26-Nov	27-Nov
		24-hour TSP	1-hour TSP	Noise		
28-Nov	29-Nov	30-Nov				
	24-hour TSP	1-hour TSP				

The schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather, etc)

#### **Air Quality Monitoring Station**

**Noise Monitoring Station** Footbridge for Ex-Harbour Road Sports Centre

CMA5b Pedestrian Plaza CMA6a WDII PRE site office

# Monitoring Frequency

Monitoring Frequency

24-hr TSP Once every 6 days 1-hr TSP 3 times every 6 days (as required in of complaints)

Once per week

M1a

### Shatin to Central Link 1123 - CEDD Entrusted Work Road P2 & other roads and Slip Road 3 **Tentative Impact Monitoring Schedule for December 2021**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			1-Dec	2-Dec	3-Dec	4-Dec
			Noise			24-hour TSP
5-Dec	6-Dec	7-Dec	8-Dec	9-Dec	10-Dec	11-Dec
	1-hour TSP	Noise			24-hour TSP	1-hour TSP
12-Dec	13-Dec	14-Dec	15-Dec	16-Dec	17-Dec	18-Dec
	Noise			24-hour TSP	1-hour TSP	
19-Dec	20-Dec	21-Dec	22-Dec	23-Dec	24-Dec	25-Dec
		24-hour TSP Noise	1-hour TSP		24-hour TSP	
26-Dec	27-Dec	28-Dec	29-Dec	30-Dec	31-Dec	
		1-hour TSP		24-hour TSP Noise		

The schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather, etc)

#### **Air Quality Monitoring Station**

**Noise Monitoring Station** Footbridge for Ex-Harbour Road Sports Centre

CMA5b Pedestrian Plaza CMA6a WDII PRE site office

# Monitoring Frequency

Monitoring Frequency

24-hr TSP Once every 6 days 1-hr TSP 3 times every 6 days (as required in of complaints)

Once per week

M1a

#### Shatin to Central Link 1123 - CEDD Entrusted Work Road P2 & other roads and Slip Road 3 Tentative Impact Monitoring Schedule for January 2022

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1-Jan
						1
						ļ
2-Jan	3-Jan	4-Jan	5-Jan	6-Jan	7-Jan	8-Jan
			24-hour TSP	1-hour TSP	Noise	
9-Jan	10-Jan	11-Jan	12-Jan	13-Jan	14-Jan	15-Jan
		24-hour TSP	1-hour TSP	Noise		
16-Jan	17-Jan	18-Jan	19-Jan	20-Jan	21-Jan	22-Jan
10-Jaii	17-Jan	10-Jali	19-Jali	20-Jan	2 I-JdII	22-Jd11
	24-hour TSP	1-hour TSP	Noise			24-hour TSP
23-Jan	24-Jan	25-Jan	26-Jan	27-Jan	28-Jan	29-Jan
	1-hour TSP	Noise			24-hour TSP	1-hour TSP
30-Jan	31-Jan					
	24-hour TSP Noise					

The schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather, etc)

#### Air Quality Monitoring Station

CMA5b Pedestrian Plaza WDII PRE site office Noise Monitoring Station M1a

Footbridge for Ex-Harbour Road Sports Centre

# CMA6a

Monitoring Frequency

Monitoring Frequency

Once per week

24-hr TSP Once every 6 days 1-hr TSP 3 times every 6 days (as required in of complaints)

### Shatin to Central Link 1123 - CEDD Entrusted Work Road P2 & other roads and Slip Road 3 Tentative Impact Monitoring Schedule for February 2022

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-Feb	2-Feb	3-Feb	4-Feb	5-Feb
					1-hour TSP	24-hour TSP
6-Feb	7-Feb	8-Feb	9-Feb	10-Feb	11-Feb	12-Feb
				1-hour TSP	24-hour TSP	Noise
13-Feb	14-Feb	15-Feb	16-Feb	17-Feb	18-Feb	19-Feb
			1-hour TSP	24-hour TSP	Noise	
20-Feb	21-Feb	22-Feb	23-Feb	24-Feb	25-Feb	26-Feb
		1-hour TSP	24-hour TSP	Noise		
27-Feb	28-Feb					
	1-hour TSP					

The schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather, etc)

#### **Air Quality Monitoring Station**

**Noise Monitoring Station** 

CMA5b Pedestrian Plaza CMA6a WDII PRE site office M1a Footbridge for Ex-Harbour Road Sports Centre

#### Monitoring Frequency

Monitoring Frequency
Once per week

24-hr TSP Once every 6 days1-hr TSP 3 times every 6 days (as required in of complaints)

## APPENDIX G

Air Quality Monitoring Results and their Graphical Presentations

#### Appendix G Air Quality Monitoring Results

	Start Time	Weather	1st Hour Conc.	2nd Hour Conc.	3rd Hour Conc.
Date	(hh:mm)	Condition	(µg/m <sup>3</sup> )	(µg/m <sup>3</sup> )	(µg/m <sup>3</sup> )
1-Nov-21	10:15	Sunny	62.6	63.4	60.9
6-Nov-21	14:20	Sunny	64.6	65.7	62.7
12-Nov-21	10:45	Sunny	66.2	64.3	65.1
18-Nov-21	13:10	Sunny	67.8	68.8	66.2
24-Nov-21	13:25	Sunny	63.7	65.2	65.9
30-Nov-21	11:45	Sunny	64.6	66.2	66.9
				Average	65.0
				Min	60.9


Max

68.8

#### 1-hour TSP Monitoring Results at Station CMA5b (Pedestrian Plaza)

#### 1-hour TSP Monitoring Results at Station CMA6a (WDII PRE Site Office)

	Start		1st Hour	2nd Hour	3rd Hour
	Time	Weather	Conc.	Conc.	Conc.
Date	(hh:mm)	Condition	(µg/m <sup>3</sup> )	(µg/m <sup>3</sup> )	(µg/m³)
1-Nov-21	10:00	Sunny	59.4	61.3	58.5
6-Nov-21	14:05	Sunny	61.1	62.2	59.5
12-Nov-21	10:30	Sunny	61.4	62.2	60.6
18-Nov-21	13:00	Sunny	61.9	63.3	64.1
24-Nov-21	13:40	Sunny	63.0	62.8	62.1
30-Nov-21	11:35	Sunny	63.3	61.6	62.2
				Average	61.7
				Min	58.5
				Max	64.1

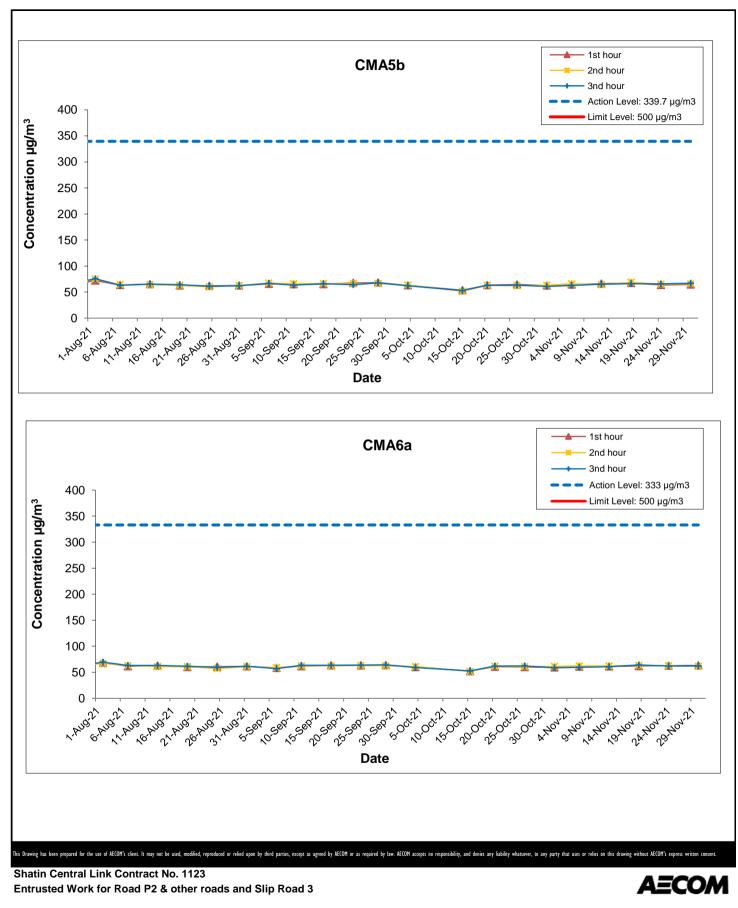

#### Graphical Presentation of Impact 1-hr TSP Monitoring Results

#### Appendix G Air Quality Monitoring Results


#### 24-hour TSP Monitoring Results at Station CMA5b (Pedestrain Plaza)

5	Start	End		Weather	Air	Atmospheric	Flow Rate (m <sup>3</sup> /min.)		Av. flow	Total vol.	I vol. Filter Weight (g)		Particulate Elapse Ti		se Time	Sampling	Conc.
Date	Time	Date	Time	Condition	Temp. (°C)	Pressure (hPa)	Initial	Final	(m³/min)	(m³)	Initial	Final	weight(g)	Initial	Final	Time(hrs.)	(µg/m³)
5-Nov-21	0:00	6-Nov-21	0:00	Sunny	25.6	1012.5	1.34	1.34	1.34	1928.2	2.6894	2.8244	0.1350	27599.01	27623.01	24.00	70.0
11-Nov-21	0:00	12-Nov-21	0:00	Sunny	21.5	1017.7	1.33	1.33	1.33	1921.0	2.7864	2.8937	0.1073	27623.01	27647.01	24.00	55.9
17-Nov-21	0:00	18-Nov-21	0:00	Sunny	23.5	1017.1	1.33	1.33	1.33	1921.0	2.6501	2.8179	0.1678	27647.01	27671.01	24.00	87.4
23-Nov-21	0:00	24-Nov-21	0:00	Sunny	17.4	1021.1	1.33	1.33	1.33	1921.0	2.7950	2.9000	0.1050	27671.01	27695.01	24.00	54.7
29-Nov-21	0:00	30-Nov-21	0:00	Sunny	21.3	1018.4	1.33	1.33	1.33	1921.0	2.6800	2.8017	0.1217	27695.01	27719.01	24.00	63.4
																Average	66.2
																Minimum	54.7
																Maximum	87.4

#### 24-hour TSP Monitoring Results at Station CMA6a (WDII PRE site office)

9	Start	End		Weather	Air	Atmospheric	Flow Rat	e (m <sup>3</sup> /min.)	Av. flow	Total vol.	Filter W	eight (g)	Particulate	Elaps	e Time	Sampling	Conc.
Date	Time	Date	Time	Condition	Temp. (°C)	Pressure (hPa)	Initial	Final	(m³/min)	(m³)	Initial	Final	weight(g)	Initial	Final	Time(hrs.)	(µg/m³)
5-Nov-21	0:00	6-Nov-21	0:00	Sunny	25.6	1012.5	1.33	1.33	1.33	1921.0	2.6759	2.7286	0.0527	10344.39	10368.39	24.00	27.4
11-Nov-21	0:00	12-Nov-21	0:00	Sunny	21.5	1017.7	1.33	1.33	1.33	1916.6	2.7953	2.8407	0.0454	10368.39	10392.39	24.00	23.7
17-Nov-21	0:00	18-Nov-21	0:00	Sunny	23.5	1017.1	1.33	1.33	1.33	1916.6	2.6540	2.7381	0.0841	10392.39	10416.39	24.00	43.9
23-Nov-21	0:00	24-Nov-21	0:00	Sunny	17.4	1021.1	1.33	1.33	1.33	1916.6	2.7935	2.8573	0.0638	10416.39	10440.39	24.00	33.3
29-Nov-21	0:00	30-Nov-21	0:00	Sunny	21.3	1018.4	1.33	1.33	1.33	1916.6	2.6676	2.7399	0.0723	10440.39	10464.39	24.00	37.7
																Average	33.2

Average	33.2
Minimum	23.7
Maximum	43.9

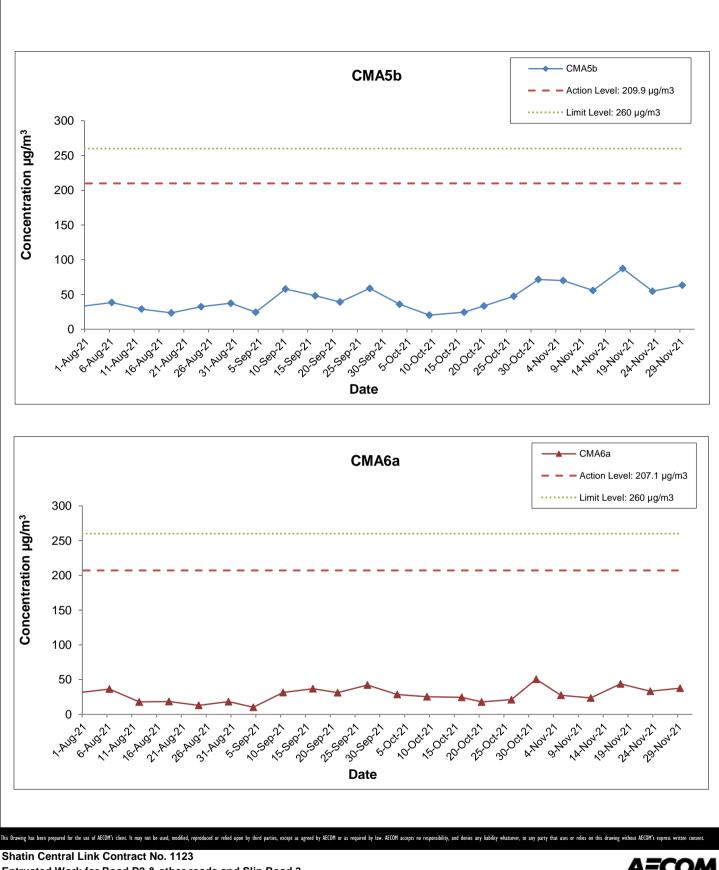



Entrusted Work for Road P2 & other roads and Slip Road 3


AECOM


Graphical Presentation of Impact 24-hr TSP Monitoring Results


Date: December 2021

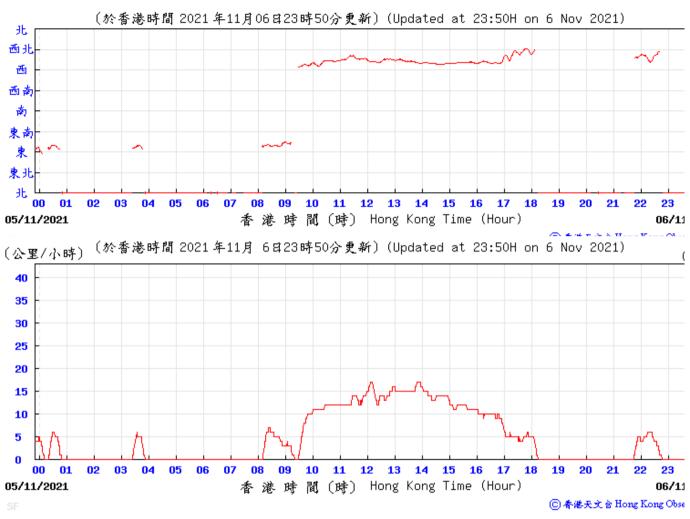

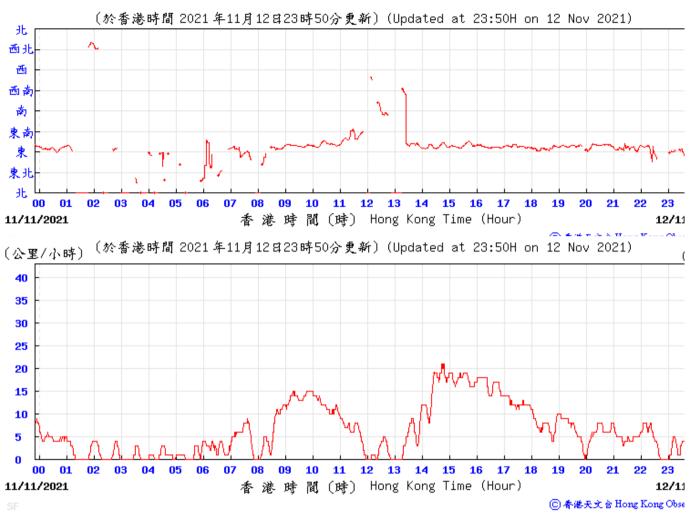

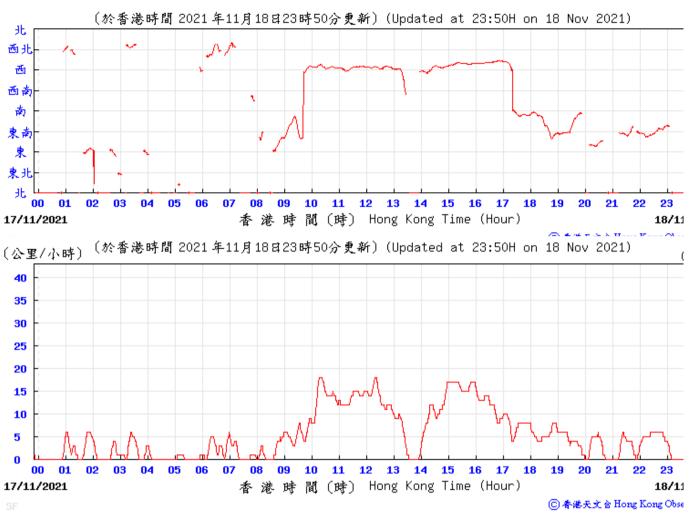

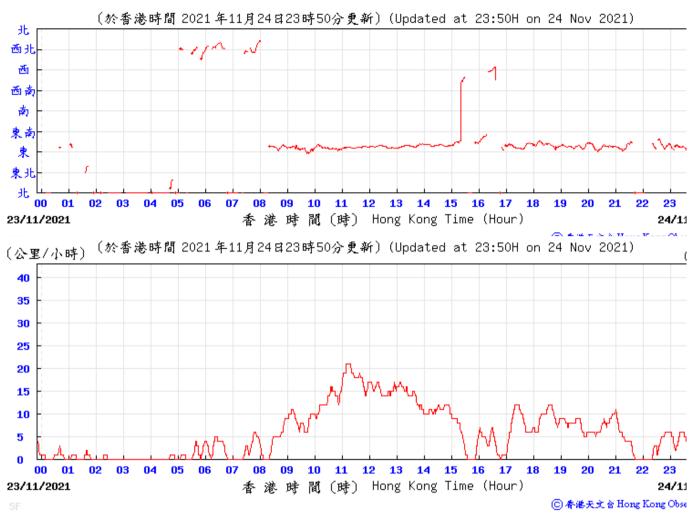

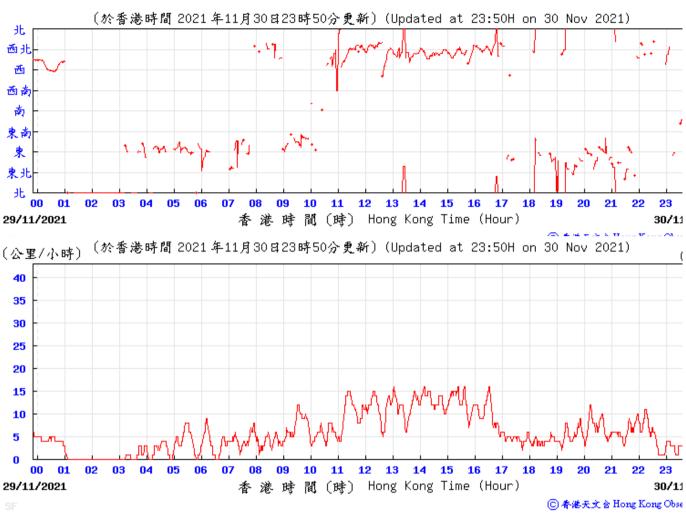

APPENDIX H


Noise Monitoring Results and their Graphical Presentations

# Appendix H Regular Construction Noise Monitoring Results

Date	Weather	Noise Level for 30-min, dB(A) <sup>+</sup>				Baseline Corrected	Baseline Noise	Limit Level,	Exceedance
Duit	Condition -		L90	L10	Leq	Level, dB(A)	Level, dB(A)	dB(A)	(Y/N)
2-Nov-21	Sunny	11:15	65.0	69.8	68.4	<baseline< td=""><td>73.0</td><td>75</td><td>N</td></baseline<>	73.0	75	N
11-Nov-21	Sunny	13:05	65.7	69.9	68.6	<baseline< td=""><td>73.0</td><td>75</td><td>N</td></baseline<>	73.0	75	N
17-Nov-21	Sunny	13:45	65.2	69.1	68.2	<baseline< td=""><td>73.0</td><td>75</td><td>N</td></baseline<>	73.0	75	N
25-Nov-21	Sunny	13:05	65.8	69.1	68.4	<baseline< td=""><td>73.0</td><td>75</td><td>N</td></baseline<>	73.0	75	N

Daytime Noise Monitoring Results at Station M1a (Footbridge for Ex-Harbour Road Sport Centre)

<sup>+</sup> - Façade measurement

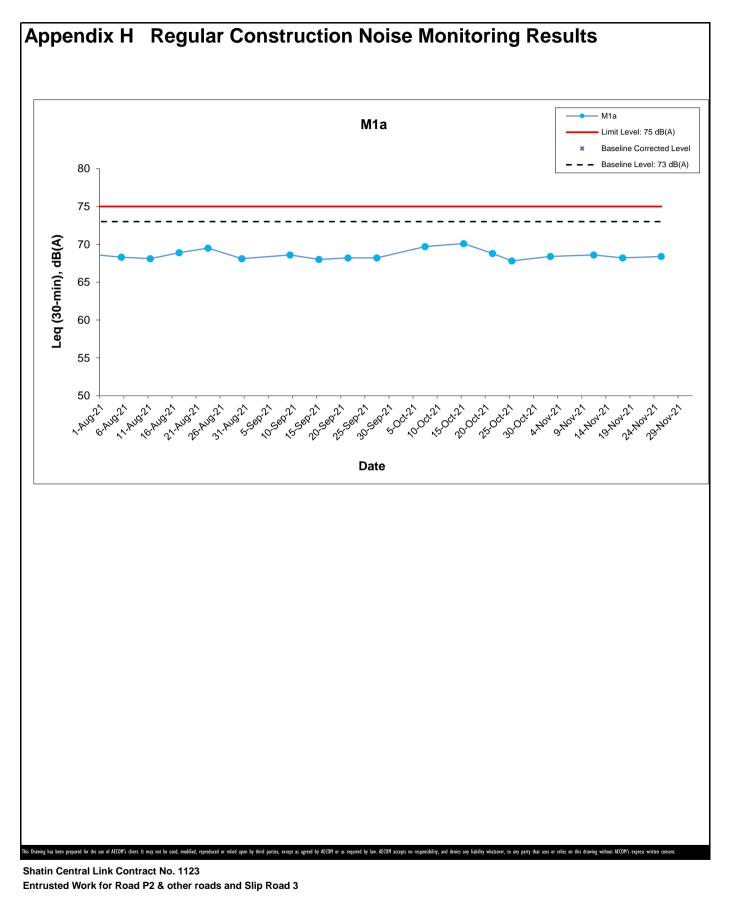

Graphical Presentation of Impact Noise Monitoring Results **APPENDIX I** 

**Event Action Plan** 

# Appendix I Event Action Plan

Event / Action Plan for Construction Dust Monitoring

EVENT		ACT	ΓΙΟΝ	
EVENI	ET	IEC	ER	Contractor
ACTION LEVEL	•			
Exceedance for one sample	<ol> <li>Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>Inform IEC and ER;</li> <li>Repeat measurement to confirm finding;</li> <li>Increase monitoring frequency to daily.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Notify Contractor.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Rectify any unacceptable practice;</li> <li>Amend working methods if appropriate.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>
Exceedance for two or more consecutive samples	<ol> <li>Identify source;</li> <li>Inform IEC and ER;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Discuss with IEC and Contractor on remedial actions required;</li> <li>If exceedance continues, arrange meeting with IEC and ER;</li> <li>If exceedance stops, cease additional monitoring.</li> <li>The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with ET and Contractor on possible remedial measures;</li> <li>Advise the ET on the effectiveness of the proposed remedial measures;</li> <li>Supervise Implementation of remedial measures.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>Ensure remedial measures properly implemented.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Submit proposals for remedial to ER within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>

		ACT	ΓΙΟΝ	
EVENT	ET	IEC	ER	Contractor
LIMIT LEVEL				
Exceedance for one sample	<ol> <li>Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>Inform ER, Contractor and EPD;</li> <li>Repeat measurement to confirm finding;</li> <li>Increase monitoring frequency to daily;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with ET and Contractor on possible remedial measures;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>Supervise implementation of remedial measures.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>Ensure remedial measures properly Implemented.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>
Exceedance for two or more consecutive samples	<ol> <li>Notify IEC, ER, Contractor and EPD;</li> <li>Identify source;</li> <li>Repeat measurement to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>If exceedance stops, cease additional monitoring.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>Supervise the implementation of remedial measures</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Ensure remedial measures properly implemented;</li> <li>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Resubmit proposals if problem still not under control;</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>

# Appendix I Event Action Plan

# Appendix I Event Action Plan

Event and Action Plan for Construction Noise Monitoring

EVENT	ACTION									
EVENT	ET	IEC	ER	Contractor						
Exceedance of Action Level	<ol> <li>Notify ER, IEC and Contractor;</li> <li>Carry out investigation;</li> <li>Report the results of investigation to the IEC, ER and Contractor;</li> <li>Discuss with the IEC and Contractor on remedial measures required;</li> <li>Increase monitoring frequency to check mitigation effectiveness.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Review the investigation results submitted by the ET;</li> <li>Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Supervise the implementation of remedial measures.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Submit noise mitigation proposals to IEC and ER;</li> <li>Implement noise mitigation proposals.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>						
Exceedance of Limit Level	<ol> <li>Inform IEC, ER, Contractor and EPD;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency;</li> <li>Identify source and investigate the cause of exceedance;</li> <li>Carry out analysis of Contractor's working procedures;</li> <li>Discuss with the IEC, Contractor and ER on remedial measures required;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>If exceedance stops, cease additional monitoring.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Supervise the implementation of remedial measures;</li> <li>If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC and ER within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Submit further proposal if problem still not under control;</li> <li>Stop the relevant portion of works as instructed by the ER until the exceedance is abated.</li> <li>(The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>						

APPENDIX J

Cumulative Statistics of Exceedances, Complaints, Notification of Summons and Successful Prosecutions

#### Leighton – China State J.V.

# Appendix J

Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

	Date Received	Subject	Status	Total no. received in this month	Total no. received since project commencement
Environmental complaints	-	-	-	0	0
Notification of summons	-	-	-	0	0
Successful Prosecutions	-	-	-	0	0

APPENDIX K

Waste Flow Table

#### MONTHLY SUMMARY WASTE FLOW TABLE

Contract No.:MTR SCL 1123 - Exhibition Station and Western Approach Tunnel (Road P2 Works) Reporting Month: November 2021

	Actu	al Quantities	of Inert C&E	) Materials G	enerated Mo	nthly	Actual	Quantities of	Monthly	Actual Quantities of Marine Dumping Monthly			
Month	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in Other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper / Cardboard Packaging	Plastics	Chemical Waste	Others, e.g. general refuse	Type 1	Type 2
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )
Jan	0.958	0.000	0.000	0.000	0.958	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Feb	0.598	0.000	0.000	0.000	0.598	0.051	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Mar	0.700	0.000	0.000	0.000	0.700	0.097	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Apr	0.741	0.000	0.000	0.000	0.741	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
May	0.176	0.000	0.000	0.000	0.176	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Jun	0.070	0.000	0.000	0.000	0.070	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Sub-total	3.243	0.000	0.000	0.000	3.243	0.148	0.000	0.000	0.000	0.000	0.000	0.000	0.000
July	0.315	0.000	0.000	0.000	0.315	0.000	0.000	0.000	0.000	0.000	0.001	0.000	0.000
August	0.525	0.000	0.000	0.000	0.525	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
September	0.112	0.000	0.000	0.000	0.112	0.000	0.000	0.000	0.000	0.000	0.011	0.000	0.000
October	0.272	0.000	0.000	0.000	0.272	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
November	0.196	0.000	0.000	0.000	0.196	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
December													
Total	4.663	0.000	0.000	0.000	4.663	0.148	0.000	0.000	0.000	0.000	0.012	0.000	0.000

#### Monthly Summary Waste Flow Table for 2021

Comments:

1) Assumption: The densities of Rock, Soil, Mixed Rock and Soil, and Regular Spoil are 2.0 ton/m<sup>3</sup>; the density of general refuse is 1.0 ton/m<sup>3</sup>; the density of waste oil is 1.0 kg/L.

2) The cut-off date of waste amount in November is 30/11/2021 for Public Fill Facilities and Landfill.

3) The amounts of waste in November is 0 ton for Landfill and 391.68 tons for Public Fill.

4) The amount of import fill in November is 0 ton, for cut-off date as 30/11/2021.

5) The amount of metal waste generated in November is 0 kg, for cut-off date as 30/11/2021.

6) The amount of paper waste generated in November is 0 kg, for cut-off date as 30/11/2021.

7) The amount of plastic waste generated in November is 0 kg, for cut-off date as 30/11/2021.
