



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

**CONTRACT NO: HK/2011/07**

**WANCHAI DEVELOPMENT PHASE II AND CENTRAL  
WANCHAI BYPASS  
SAMPLING, FIELD MEASUREMENT AND TESTING WORK  
(STAGE 2)**

**ENVIRONMENTAL PERMIT NO. EP- 416/2011 AND FEP-  
01/416/2011**

**SHATIN TO CENTRAL LINK (SCL) PROTECTION WORKS AT  
CAUSEWAY BAY TYPHOON SHELTER (CBTS)**

**MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT**

**- DECEMBER 2014 -**

**CLIENTS:**

**Civil Engineering and Development  
Department**

**and**

**Highways Department**

**PREPARED BY:**

**Lam Geotechnics Limited**

11/F Centre Point  
181-185 Gloucester Road,  
Wanchai, H.K.

Telephone: (852) 2882-3939  
Facsimile: (852) 2882-3331  
E-mail: [info@lamenviro.com](mailto:info@lamenviro.com)  
Website: <http://www.lamenviro.com>

**CERTIFIED BY:**

Raymond Dai  
Environmental Team Leader

**DATE:**

12 January 2015

Ref.: AACWBIECEM00\_0\_6131L.15

12 January 2015

By Post and Fax (2691 2649)

AECOM Asia Company Limited  
11/F, Tower 2  
Grand Central Plaza  
138 Shatin Rural Committee Road  
Shatin, New Territories  
Hong Kong

Attention: Mr. Conrad Ng

Dear Sir,

**Re: Shatin to Central Link – Protection Works at Causeway Bay Typhoon Shelter**  
**Monthly Environmental Monitoring and Audit Report (December 2014)**  
**for EP-416/2011 & FEP-01/416/2011**

Reference is made to the Environmental Team's submission of the captioned Monthly Environmental Monitoring and Audit (EM&A) Report for December 2014 received by email 12 January 2015.

Please be informed that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 in the captioned Environmental Permit.

Thank you very much for your kind attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,



David Yeung  
Independent Environmental Checker

c.c.	HyD	Mr. Cyrus Wong	by fax: 2761 1508
	HyD	Mr. Eddy Wu	by fax: 2714 5289
	CEDD	Mr. Jason Cheung	by fax: 2577 5040
	AECOM	Mr. Peter Poon	by fax: 3912 3010
	AECOM	Mr. Frankie Fan	by fax: 2587 1877
	MTRCL	Mr. Richard Kwan	by fax: 2993 7577
	Lam	Mr. Raymond Dai	by fax: 2882 3331

Q:\Projects\AACWBIECEM00\Corr\AACWBIECEM00\_0\_6131L.15.doc



## TABLE OF CONTENTS

<b>EXECUTIVE SUMMARY .....</b>	<b>3</b>
<b>1 INTRODUCTION.....</b>	<b>5</b>
1.1 Scope of the Report .....	5
1.2 Structure of the Report .....	5
<b>2 PROJECT BACKGROUND .....</b>	<b>7</b>
2.1 Background .....	7
2.2 Scope of the Project and Site Description .....	7
2.3 Project Organization and Contact Personnel .....	8
<b>3 STATUS OF REGULATORY COMPLIANCE .....</b>	<b>9</b>
3.1 Status of Environmental Licensing and Permitting under the Project .....	10
<b>4 MONITORING REQUIREMENTS .....</b>	<b>12</b>
4.1 Noise Monitoring .....	12
4.2 Air quality monitoring .....	13
4.3 Water Quality Monitoring .....	14
<b>5 MONITORING RESULTS .....</b>	<b>18</b>
5.1 Noise Monitoring Results .....	18
5.2 Air quality monitoring Results .....	18
5.3 Water quality monitoring Results .....	18
5.4 Waste Monitoring Results .....	20
<b>6 COMPLIANCE AUDIT .....</b>	<b>21</b>
6.1 Noise Monitoring .....	21
6.2 Air quality monitoring .....	21
6.3 Water quality monitoring .....	21
6.4 Review of the Reasons for and the Implications of Non-compliance .....	21
6.5 Summary of action taken in the event of and follow-up on non-compliance .....	21
<b>7 CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS .....</b>	<b>22</b>
<b>8 ENVIRONMENTAL SITE AUDIT .....</b>	<b>25</b>
<b>9 COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION .....</b>	<b>27</b>
<b>10. CONCLUSION .....</b>	<b>28</b>



## LIST OF TABLES

<b>Table I</b>	<b>Summary of Water Quality Monitoring Exceedances in Reporting Month</b>
<b>Table 2.1</b>	<b>Schedule 2 Designated Projects under this Project</b>
<b>Table 2.2</b>	<b>Contact Details of Key Personnel</b>
<b>Table 3.1</b>	<b>Summary of the current status on licences and/or permits on environmental protection pertinent to the Project</b>
<b>Table 3.2</b>	<b>Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/15</b>
<b>Table 3.3</b>	<b>Summary of submission status under EP/416/2011 and FEP-01/416/2011</b>
<b>Table 4.1</b>	<b>Noise Monitoring Stations</b>
<b>Table 4.2</b>	<b>Air quality monitoring Stations</b>
<b>Table 4.3</b>	<b>Marine Water Quality Stations for Water Quality Monitoring</b>
<b>Table 4.4</b>	<b>Marine Water Quality Monitoring Frequency and Parameters</b>
<b>Table 5.1</b>	<b>Noise Monitoring Station</b>
<b>Table 5.2</b>	<b>Air quality monitoring Station</b>
<b>Table 5.3</b>	<b>Water quality monitoring Station</b>
<b>Table 5.4</b>	<b>Summary of Water Quality Monitoring Exceedance in Reporting Month</b>
<b>Table 5.5</b>	<b>Details of Waste Disposal</b>
<b>Table 8.1</b>	<b>Summary of Environmental Inspection for Contract no. HY/2009/15</b>
<b>Table 9.1</b>	<b>Cumulative Statistics on Complaints</b>
<b>Table 9.2</b>	<b>Cumulative Statistics on Successful Prosecutions</b>
<b>Table 10.1</b>	<b>Summary of Key Construction Activities of Individual Contract(s) to be commenced in Coming Reporting Month</b>

## LIST OF FIGURES

<u>Figure 2.1</u>	Project Layout
<u>Figure 2.2</u>	Project Organization Chart
<u>Figure 2.3</u>	Locations of Environmental Monitoring Stations

## LIST OF APPENDICES

<u>Appendix 3.1</u>	Environmental Mitigation Implementation Schedule
<u>Appendix 4.1</u>	Action and Limit Level
<u>Appendix 4.2</u>	Copies of Calibration Certificates
<u>Appendix 5.1</u>	Monitoring Schedule for Reporting Month and Coming month
<u>Appendix 5.2</u>	Noise Monitoring Results and Graphical Presentations
<u>Appendix 5.3</u>	Air Quality Monitoring Results and Graphical Presentations
<u>Appendix 5.4</u>	Water Quality Monitoring Results and Graphical Presentations
<u>Appendix 6.1</u>	Event Action Plans
<u>Appendix 6.2</u>	Summary of Notification of Exceedances
<u>Appendix 7.1</u>	Complaint Log
<u>Appendix 8.1</u>	Construction Programme of Individual Contracts



---

## EXECUTIVE SUMMARY

- i. This is the Environmental Monitoring and Audit (EM&A) Monthly Report – [December 2014](#) specific for Environmental Permit no. EP-416/2011 and Further Environmental Permit no. FEP-01/416/2011 on Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter (CBTS). The Shatin to Central Link (SCL) protection works inside the Causeway Bay Typhoon Shelter (CBTS) is entrusted to the Central-Wanchai Bypass (CWB) project and will be carried out concurrently with the construction of the CWB under contract no. HY/2009/15. The construction impact of the SCL protection works on the environment is monitored together with that of the CWB by the Environmental Team (ET) employed under Contractor No. HK/2011/07. This EM&A report captures the environmental monitoring findings and information recorded during the period [November 2014 to December 2014](#). The cut-off date of reporting is on the 27th of each reporting month.
- ii. In the reporting period, the principal work activity is included as follows:
  - [Installation of seawall blocks and backfilling works for formation of TZ4](#)
  - [Reinstatement of existing bermstone and seawall](#)
  - [Post tunnel construction works at ME4](#)

### Noise Monitoring

- iii. Noise monitoring during daytime was conducted at M2b - Noon gun area on a weekly basis.
- iv. [No action or limit level exceedance was recorded at M2b – Noon gun area in the reporting period.](#)

### Air quality monitoring

- v. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted at CMA3a - CWB PRE Site Office Area.
- vi. [No action or limit level exceedance was recorded in the reporting period.](#)
- vii. [Due to interruption of electricity, the 24hr TSP was rescheduled 8 December 2014 and 13 December 2014 to 9 December 2014 and 15 December 2014 respectively.](#)

### Water Quality monitoring

- viii. Water quality monitoring at C7 was conducted three days per week during the reporting period. The action and limit level exceedance of water quality monitoring are summarized in ***Table I.***
- ix. [As confirmed by CWB RSS, the operation of the pump station for Windsor House Cooling Water was suspended from 22 Oct 2014 for the Windsor House intake cooling intake diversion scheme and temporary supply of freshwater from WSD water mains was provided to cooling water intake. The water quality monitoring for the respective cooling water intake at WQM station C7 was temporarily suspended from 22 Oct 2014.](#)

- x. As informed by CWB RSS, the operation of the diverted Windsor House cooling intake was commenced on 20 Dec 2014 and the water quality monitoring at monitoring station C7 for Windsor House Cooling water intake was resumed on 22 Dec 2014.
- xi. No action or limit level exceedance was recorded in the reporting period.

**Table I Summary of Water Quality Monitoring Exceedances in Reporting Month**

Contract no.	Water quality monitoring Station	Mid-flood						Mid-ebb					
		DO		Turbidity		SS		DO		Turbidity		SS	
		AL	LL	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL
HY/2009/15	C7	0	0	0	0	0	0	0	0	0	0	0	0
<b>Total</b>		0	0	0	0	0	0	0	0	0	0	0	0

Complaints, Notifications of Summons and Successful Prosecutions

- xii. There was no complaint received in this reporting period.

Site Inspections and Audit

- xiii. The Environmental Team (ET) conducted weekly site inspections for Contract no. HY/2009/15 - Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter (CBTS), in this reporting period. No non-conformance was identified during the site inspections.

Future Key Issues

- xiv. In coming reporting month, the principal work activity is anticipated as follows:
- Installation of seawall blocks and backfilling works for formation of TZ4
  - Jetty beams construction for permanent RHKYC jetty
  - Reinstatement of existing bermstone and seawall
  - Post tunnel construction works at ME4

## **1 INTRODUCTION**

### **1.1 Scope of the Report**

- 1.1.1. Lam Geotechnics Limited (LGL) has been appointed to work as the Environmental Team (ET) under Environmental Permit no. EP-416/2011 and Further Environmental permit nos. FEP-01/416/2011 to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter (CBTS) (Register No.: AEIAR-159/2011) and in the EM&A Manual of the approved EIA Report for Shatin to Central Link Protection Works at Causeway Bay Typhoon Shelter (Register No. AEIAR-159/2011).
- 1.1.2. This report presents the environmental monitoring and auditing work carried out in accordance to the Section 7.5 of EM&A Manual and Environmental Monitoring and Audit Requirements of Environmental permit nos. EP-416/2011 and Further Environmental permit nos. FEP-01/416/2011.
- 1.1.3. This report documents the finding of EM&A works for Environmental Permit (EP) no. EP-416/2011, Further Environmental Permit (FEP) nos. FEP-01-416/2011 during the period [November 2014 to December 2014](#). The cut-off date of reporting is at 27<sup>th</sup> of each reporting month.

### **1.2 Structure of the Report**

- Section 1**      ***Introduction*** – details the scope and structure of the report.
- Section 2**      ***Project Background*** – summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.
- Section 3**      ***Status of Regulatory Compliance*** – summarizes the status of valid Environmental Permits / Licenses during the reporting period.
- Section 4**      ***Monitoring Requirements*** – summarizes all monitoring parameters, monitoring methodology and equipment, monitoring locations, monitoring frequency, criteria and respective event and action plan and monitoring programmes.
- Section 5**      ***Monitoring Results*** – summarizes the monitoring results obtained in the reporting period.
- Section 6**      ***Compliance Audit*** – summarizes the auditing of monitoring results, all exceedances environmental parameters.



**Section 7**      ***Cumulative Construction Impact due to the Concurrent Projects*** – summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.

**Section 8**      ***Site Inspection*** – summarizes the findings of weekly site inspections undertaken within the reporting period, with a review of any relevant follow-up actions within the reporting period.

**Section 9**      ***Complaints, Notification of summons and Prosecution*** – summarizes the cumulative statistics on complaints, notification of summons and prosecution

**Section 10**     ***Conclusion***

## **2 PROJECT BACKGROUND**

### **2.1 Background**

- 2.1.1. The “Shatin to Central Link Protection Works at Causeway Bay Typhoon Shelter” (hereafter called “the Project”) is a Designed Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Reports for Shatin to Central Link Protection Works at CBTS (Register No. AEIAR-159/2011) has been approved on 25 Feb 2011.
- 2.1.2. The key purpose of the SCL Protection Works and associated works at CBTS involves the construction of a 160m tunnel box by cut-and-cover method at the crossing above the Central – Wan Chai Bypass (CWB) tunnels. Temporary reclamation is required and has been authorized under the Foreshore and Sea-bed (reclamations) Ordinance. With the presence of the Protection Works, future construction of the SCL on both sides of the CWB tunnels is protected and ensured feasible without damaging or unduly affecting the CWB tunnels which could be operational by then. This arrangement will also minimize public nuisance and impact to the surrounding environment as it can reduce the reclamation area for subsequent construction of the SCL after CWB is completed. Nevertheless, the Protection Works cannot serve to function for any railway service or operation before the completion of SCL.
- 2.1.3. The SCL is strategically important for connecting the existing railway lines into an integrated rail network. The east-west connection will allow the setup of a 57km East-West Corridor across the city connecting Wu Kai Sha with Tuen Mun via Kowloon; whilst the north-south connection will operate over a 41km North-South Corridor with services originating in Lok Ma Chau or Lo Wu travelling via the existing East Rail Line (EAL) to Admiralty. This will enable a direct transportation linkage between Mainland China and Hong Kong Island.

### **2.2 Scope of the Project and Site Description**

- 2.2.1. The study area encompasses existing developments in Causeway Bay Typhoon Shelter as shown in **Figure 2.1**. The scope of the Project includes:
- Temporary reclamation, which occupies about 0.7ha of Government foreshore and sea-bed (of which 0.3ha is already authorized under CWB project, i.e. additional reclamation of 0.4ha is required).
  - Dredging works at the southeast corner of the CBTS to provide space for temporary relocation of anchorage area due to the additional temporary reclamation for the Project.
  - Construction of a section of the twin track railway tunnel structure (approximately 160m long) above the proposed CWB located entirely offshore within the CBTS.
  - Relocation of the temporary Royal Hong Kong Yacht Club (RHKYC) jetty within the CWB temporary reclamation to a new location.

- Removal of the temporary reclamation, except the small area at the southwest corner of the reclamation (which will be removed by the SCL project upon completion of the future SCL tunnels connecting to the proposed South Ventilation Building (SOV)).

2.2.2. The Project contains Schedule 2 DP that, under the EIAO, requires Environmental Permits (EPs) to be granted by the DEP before they may either be constructed or operated. **Table 2.1** summarises the DP under this Project. [Figure 2.1](#) shows the location of this Schedule 2 DP.

**Table 2.1 Schedule 2 Designated Projects under this Project**

Item	Designated Project	EIAO Reference	Reason for inclusion
DP1	Temporary reclamation, which occupies about 0.7ha of Government foreshore and sea-bed	Schedule 2, Part I, C.12	A dredging operation which is less than 100m from a seawater intake point

### 2.3 Project Organization and Contact Personnel

2.3.1 Civil Engineering and Development Department and Highways Department are the overall project controllers for the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.

2.3.2 The proposed project organization and lines of communication with respect to environmental protection works are shown in **Figure 2.2**. Key personnel and contact particulars are summarized in **Table 2.2**

**Table 2.2 Contact Details of Key Personnel**

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Principal Resident Engineer	Mr. Frankie Fan	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3912 3388	3912 3010
MTR Corporation Limited	Permit Holder	Environment Manager	Mr. Richard Kwan	2688 1179	2993 7577
		Environmental Engineer I	Miss. Viola Tong	3127 6296	
		Environmental Engineer II	Mr. Chris Mak	3127 6297	
China State Construction Engineering (HK) Ltd.	Contractor under Contract no. HY/2009/15	Project Director	Mr. K C Cheung	3557 6399	2566 2192
		Site Manager	Mr. J H Chen	3557 6368	
		Contractor's Representative	Mr. Gene Cheung	3557 6407	
		Head of construction	Mr. Roger Cheung	3557 6371	
		Environmental Officer	Mr. Andy Mak	3557 6347	
ENVIRON Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	3465 2888	3465 2899
Lam Geotechnics Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331

2.3.3 In this reporting period, the principal work activity is included as follows:

- Installation of seawall blocks and backfilling works for formation of TZ4
- Reinstatement of existing bermstone and seawall
- Post tunnel construction works at ME4

2.3.4 In coming reporting month, the principal work activity is anticipated as follows:

- Installation of seawall blocks and backfilling works for formation of TZ4
- Jetty beams construction for permanent RHKYC jetty
- Reinstatement of existing bermstone and seawall
- Post tunnel construction works at ME4

### 3 STATUS OF REGULATORY COMPLIANCE

#### 3.1 Status of Environmental Licensing and Permitting under the Project

3.1.1. A summary of the current status on licences and/or permits on environmental protection pertinent to the Project is shown in **Table 3.1**.

**Table 3.1 Summary of the current status on licences and/or permits on environmental protection pertinent to the Project**

Permits and/or Licences	Reference No.	Issued Date	Status
Environmental Permit	EP-416/2011	4 April 2011	Valid
Further Environmental Permit	FEP-01/416/2011	11 Nov 2011	Valid

3.1.2. Summary of the current status on licences and/or permits on environmental protection pertinent and submission under FEP-01/416/2011 for contract no. HY/2009/15 showed in Table 3.2 and Table 3.3.

**Table 3.2 Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/15**

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-01/416/2011	11 Nov 2011	N/A	Valid
Notification of Works Under APCO	321822	24 Sep 2010	N/A	Valid
Construction Noise Permit (CNP) for D-wall and seawall removal works at TS4/ME4	GW-RS0721-14	16 Jul 2014	18 Jul 2014 to 15 Jan 2015	Valid
Registration as a Chemical Waste Producer	WPN: 5213-147-C1169-35	15 Nov 2010	N/A	Valid
Billing Account under Waste Disposal Ordinance	7011553	30 Sep 2010	27 Sep 2010 to 27 Jan 2016	Valid
Billing Account under Waste Disposal Ordinance (Disposal by Vessel)	7011761	7 Oct 2014	17 Oct 2014 to 16 Jan 2015	Valid
Water Discharge Licence (Discharge at TS4)	WT00018542-2014	17 Mar 2014	17 Mar 2014 to 31 Jan 2016	Valid
Dumping Permit (Type 1 – Open Sea Disposal)	EP/MD/15-063	16 Jul 2014	28 Jul 2014 to 27 Jan 2015	Valid



**Table 3.3 Summary of submission status under EP/416/2011 and FEP-01/416/2011**

EP Condition	FEP Condition	Submission	Date of Submission
2.3	2.1	Notification of setting up of ENPC	Submitted to EPD on 21 Nov 2011
2.4	-	Notification of setting up of CLG	Submitted to EPD on 21 Nov 2011
2.5	2.2	Notification of work commencement date	Submitted to EPD on 21 Oct 2011
2.5	-	Organization chart	Submitted to EPD on 17 Oct 2011
2.6	2.2	Work schedule and Location Plans	Submitted to EPD on 27 Oct 2011
2.7	2.3	Silt Curtain Deployment Plan	Re-submitted to EPD on 15 Dec 2011
2.8	2.4	Silt Screen Deployment Plan	Re-submitted to EPD on 15 Dec 2011
3.3	-	Baseline Monitoring Report	Submitted to EPD on 14 Nov 2011

## 4 Monitoring Requirements

### 4.1 Noise Monitoring

#### NOISE MONITORING STATIONS

- 4.1.1. The noise monitoring stations for the Project are listed and shown in **Table 4.1** and [Figure 2.3](#). [Appendix 4.1](#) shows the established Action/Limit Levels for the monitoring works.

**Table 4.1 Noise Monitoring Stations**

Station	Description
M2b	Noon Gun Area

#### NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.1.2. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ).  $L_{eq}$  (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods,  $L_{eq}$  (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. Supplementary information for data auditing, statistical results such as  $L_{10}$  and  $L_{90}$  shall also be obtained for reference.
- 4.1.3. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
- One set of measurements between 0700 and 1900 hours on normal weekdays.

#### MONITORING EQUIPMENT

- 4.1.4. As referred to in the Technical Memorandum (TM) issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.
- 4.1.5. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

## 4.2 Air quality monitoring

### AIR QUALITY MONITORING STATIONS

- 4.2.1. The air quality monitoring stations for the Project are listed and shown in **Table 4.2** and **Figure 2.3. Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

**Table 4.2 Air quality monitoring Stations**

Station ID	Monitoring Location	Description
CMA3a	CWB PRE Site Office	Causeway Bay

### AIR QUALITY MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 4.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.
- 4.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.

### SAMPLING PROCEDURE AND MONITORING EQUIPMENT

- 4.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:
- 0.6 – 1.7 m<sup>3</sup> per minute adjustable flow range;
  - Equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
  - Installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
  - Capable of providing a minimum exposed area of 406 cm<sup>2</sup>;
  - Flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
  - Equipped with a shelter to protect the filter and sampler;
  - Incorporated with an electronic mass flow rate controller or other equivalent devices;
  - Equipped with a flow recorder for continuous monitoring;
  - Provided with a peaked roof inlet;
  - Incorporated with a manometer;

- Able to hold and seal the filter paper to the sampler housing at horizontal position;
- Easily changeable filter; and
- Capable of operating continuously for a 24-hour period.

4.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

#### LABORATORY MEASUREMENT / ANALYSIS

4.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.

4.2.8. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.

4.2.9. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.

4.2.10. All the collected samples shall be kept in a good condition for 6 months before disposal.

4.2.11. Current calibration certificates of equipments are presented in **Appendix 4.2**.

### **4.3 Water Quality Monitoring**

4.3.1. The EIA Report has identified that the key water quality impact would be associated with the dredging works during the construction phase. Marine water quality monitoring for dissolved oxygen (DO), suspended solid (SS) and turbidity is therefore recommended to be carried out at selected WSD flushing water intakes. The impact monitoring should be carried out during the proposed dredging works to ensure the compliance with the water quality standards.

#### Water Quality Monitoring Station

4.3.2. It is proposed to monitor the water quality at one cooling water intakes along the seafront of the Victoria Harbour. The proposed water quality monitoring stations of the Project are shown in **Table 4.3** and **Figure 2.3**. **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

**Table 4.3 Marine Water Quality Stations for Water Quality Monitoring**

Cooling Water Intake			
Station ID	Monitoring Location	Easting	Northing
C7	Windsor House	837193.7	816150.0

#### WATER QUALITY PARAMETERS

- 4.3.3. Monitoring of dissolved oxygen (DO), turbidity and suspended solids (SS) shall be carried out at WSD flushing water intakes and cooling water intakes. DO and Turbidity are measured in-situ while SS is determined in laboratory.
- 4.3.4. In association with the water quality parameters, other relevant data shall also be measured, such as monitoring location/position, time, sampling depth, water temperature, pH, salinity, dissolved oxygen (DO) saturation, weather conditions, sea conditions, tidal stage, and any special phenomena and work underway at the construction site etc.

#### SAMPLING PROCEDURES AND MONITORING EQUIPMENT

- 4.3.5. The interval between two sets of monitoring should not be less than 36 hours except where there are exceedances of Action and/or Limit Levels, in which case the monitoring frequency will be increased. **Table 4.4** shows the proposed monitoring frequency and water quality parameters. Duplicate in-situ measurements and water sampling should be carried out in each sampling event. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.

**Table 4.4 Marine Water Quality Monitoring Frequency and Parameters**

Activities	Monitoring Frequency <sup>1</sup>	Parameters <sup>2</sup>
During the 4-week baseline monitoring period	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
During marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
After completion of marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity

Notes:

- For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.
- Turbidity should be measured in situ whereas SS should be determined by laboratory.

---

#### DISSOLVED OXYGEN AND TEMPERATURE MEASURING EQUIPMENT

- 4.3.6. The instrument should be a portable, weatherproof dissolved oxygen measuring instrument complete with cable, sensor, comprehensive operation manuals, and use a DC power source. It should be capable of measuring:
- a dissolved oxygen level in the range of 0-20 mg/l and 0-200% saturation
  - a temperature of 0-45 degree Celsius
- 4.3.7. It should have a membrane electrode with automatic temperature compensation complete with a cable. Sufficient stocks of spare electrodes and cables should be available for replacement where necessary. (e.g. YSI model 59 meter, YSI 5739 probe, YSI 5795A submersible stirrer with reel and cable or an approved similar instrument).
- 4.3.8. Should salinity compensation not be build-in in the DO equipment, in-situ salinity shall be measured to calibrate the DO equipment prior to each DO measurement.

#### TURBIDITY MEASUREMENT INSTRUMENT

- 4.3.9. The instrument should be a portable, weatherproof turbidity-measuring instrument complete with comprehensive operation manual. The equipment should use a DC power source. It should have a photoelectric sensor capable of measuring turbidity between 0-1000 NTU and be complete with a cable (e.g. Hach model 2100P or an approved similar instrument).

#### SAMPLER

- 4.3.10. A water sampler comprises a transparent PVC cylinder, with a capacity of not less than 2 litres, and can be effectively sealed with latex cups at both ends. The sampler should have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth (e.g. Kahlsico Water Sampler or an approved similar instrument).

#### SAMPLE CONTAINER AND STORAGE

- 4.3.11. Water samples for suspended solids measurement should be collected in high-density polythene bottles, packed in ice (cooled to 4°C without being frozen), and delivered to ALS Technichem (HK) Pty Ltd. as soon as possible after collection for analysis.

#### WATER DEPTH DETECTOR

- 4.3.12. A portable, battery-operated echo sounder shall be used for the determination of water depth at each designated monitoring station. This unit can either be handheld or affixed to the bottom of the workboat, if the same vessel is to be used throughout the monitoring programme.

#### SALINITY

- 4.3.13. A portable salinometer capable of measuring salinity in the range of 0-40 ppt shall be provided for measuring salinity of the water at each of monitoring location.

---

#### MONITORING POSITION EQUIPMENT

- 4.3.14. A hand-held or boat-fixed type digital Global Positioning System (GPS) with waypoint bearing indication or other equivalent instrument of similar accuracy shall be provided and used during monitoring to ensure the monitoring vessel is at the correct location before taking measurements.

#### CALIBRATION OF IN-SITU INSTRUMENTS

- 4.3.15. All in-situ monitoring instrument shall be checked, calibrated and certified by a laboratory accredited under HOKLAS or equivalent before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the water quality monitoring. Responses of sensors and electrodes should be checked with certified standard solutions before each use. Wet bulb calibration for a DO meter shall be carried out before measurement at each monitoring location.
- 4.3.16. For the on site calibration of field equipment by the ET, the BS 127:1993, "Guide to Field and on-site test methods for the analysis of waters" should be observed.
- 4.3.17. Sufficient stocks of spare parts should be maintained for replacements when necessary. Backup monitoring equipment shall also be made available so that monitoring can proceed uninterrupted even when some equipment is under maintenance, calibration, etc.
- 4.3.18. Current calibration certificates of equipments are presented in [Appendix 4.2](#).

#### LABORATORY MEASUREMENT / ANALYSIS

- 4.3.19. Analysis of suspended solids has been carried out in a HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd. Water samples of about 1L shall be collected at the monitoring stations for carrying out the laboratory SS determination. The SS determination work shall start within 24 hours after collection of the water samples. The SS determination shall follow APHA 19ed or equivalent methods subject to the approval of IEC and EPD.

## 5 MONITORING RESULTS

5.0.1. Overall layout showing work area, latest status of work commencement and monitoring stations is shown in [Figure 2.1](#) and [Figure 2.3](#).

5.0.2. The environment monitoring schedules for reporting month and coming month are presented in [Appendix 5.1](#).

### 5.1 Noise Monitoring Results

The noise monitoring station is shown in **Table 5.1** below.

**Table 5.1 Noise Monitoring Station**

Station	Description
M2b	Noon Gun Area

5.1.1 No action or limit level exceedance at M2b – Noon Gun Area was recorded in the reporting month.

5.1.2 Details of noise monitoring results and graphical presentation can be referred in [Appendix 5.2](#)

### 5.2 Air quality monitoring Results

The air quality monitoring station is shown in **Table 5.2** below.

**Table 5.2 Air quality monitoring Station**

Station	Description
CMA3a	CWB PRE Site Office

5.2.1 No action or limit level exceedance was recorded at CMA3a CWB PRE Site Office in the reporting month.

5.2.2 Air quality monitoring results in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in [Appendix 5.3](#).

### 5.3 Water quality monitoring Results

5.3.1 The water quality monitoring station is summarized in Table 5.3 below.

**Table 5.3 Water quality monitoring Station**

Station Ref.	Location	Easting	Northing
Cooling Water Intake			
C7	Windsor House	837193.7	816150.0



- 5.3.2 Water quality monitoring location at C7 was finely adjusted to the outside of the inner sil curtain frame since 31 Dec 2012.
- 5.3.3 As confirmed by CWB RSS, the operation of the pump station for Windsor House Cooling Water was suspended from 22 Oct 2014 for the Windsor House intake cooling intake diversion scheme and temporary supply of freshwater from WSD water mains was provided to cooling water intake. The water quality monitoring for the respective cooling water intake at WQM station C7 was temporarily suspended from 22 Oct 2014.
- 5.3.4 As informed by CWB RSS, the operation of the diverted Windsor House cooling intake was commenced on 20 Dec 2014 and the water quality monitoring at monitoring station C7 for Windsor House Cooling water intake was resumed on 22 Dec 2014.
- 5.3.5 No action or limit level exceedance was recorded in this reporting month.
- 5.3.6 Water quality monitoring results measured in this reporting period are reviewed and summarized. Details of water quality monitoring results and graphical presentation can be referred in Table 5.4 and Appendix 5.4.

**Table 5.4 Summary of Water Quality Monitoring Exceedance in Reporting Month**

Contract no.	Water quality monitoring Station	Mid-flood						Mid-ebb					
		DO		Turbidity		SS		DO		Turbidity		SS	
		AL	LL	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL
HY/2009/15	C7	0	0	0	0	0	0	0	0	0	0	0	0
<b>Total</b>		0	0	0	0	0	0	0	0	0	0	0	0

## 5.4 Waste Monitoring Results

5.4.1. Inert C&D wastes were disposed of in this reporting month. Details of the waste flow table are summarized in **Table 5.5**.

**Table 5.5 Details of Waste Disposal**

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds	Remarks
Inert C&D materials disposed, m3	NIL NIL	32,670 6,267	TM38 TKO137	N/A
Inert C&D materials recycled, m3	NIL NIL NIL NIL NIL	25,395.7 1,228 1416 352 1,049	TS2 WDII Lun Ku Tan WENT Landfill HY/2011/03 (HZM)	N/A
Non-inert C&D materials disposed, m3	NIL	NIL	N/A	N/A
Non-inert C&D materials recycled, m3	NIL	NIL	N/A	N/A
Chemical waste disposed, kg	NIL	NIL	N/A	N/A
Marine Sediment (Type 1 – Open Sea Disposal) , m3	NIL (Bulk Volume)	10,640 (Bulk Volume)	Cheung Chau South	Dredging from SCL Protection Works (CBTS)
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m3	NIL (Bulk Volume)	7,500 (Bulk Volume)	East of Sha Chau	Dredging from SCL Protection Works (CBTS)
Marine Sediment (Type 3 – Special Treatment / Disposal contained in geosynthetic Containers), m3	NIL	NIL	N/A	N/A

---

**6 Compliance Audit**

6.0.1. The Event Action Plan for construction noise, air qualities are presented in [Appendix 6.1](#).

**6.1 Noise Monitoring**

6.1.1. [No exceedance was recorded at M2b – Noon Gun Area in the reporting month.](#)

**6.2 Air quality monitoring**

6.2.1 [No exceedance was recorded at CMA3a – CWB PRE Site Office in the reporting month.](#)

**6.3 Water quality monitoring**

6.3.1 [As confirmed by CWB RSS, the operation of the pump station for Windsor House Cooling Water was suspended from 22 Oct 2014 for the Windsor House intake cooling intake diversion scheme and temporary supply of freshwater from WSD water mains was provided to cooling water intake The water quality monitoring for the respective cooling water intake at WQM station C7 was temporarily suspended from 22 Oct 2014.](#)

6.3.2 [As informed by CWB RSS, the operation of the diverted Windsor House cooling intake was commenced on 20 Dec 2014 and the water quality monitoring at monitoring station C7 for Windsor House Cooling water intake was resumed on 22 Dec 2014.](#)

6.3.3 [No exceedance was recorded at C7- Windsor House Cooling Water Intake in the reporting month.](#)

**6.4 Review of the Reasons for and the Implications of Non-compliance**

6.4.1. There was no non-compliance from the site audits in the reporting period. The observations and recommendations made in each individual site audit session were presented in Section 8.

**6.5 Summary of action taken in the event of and follow-up on non-compliance**

6.5.1 There was no particular action taken since no project-related non-compliance was recorded from the site audits and environmental monitoring in the reporting period.

## **7 Cumulative Construction Impact due to the Concurrent Projects**

7.0.1. According to Condition 3.4 of the EP-416/2011, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Wan Chai Development Phase II (WDII) and Central-WanChai Bypass (CWB).

7.0.2. From the [Monthly EM&A report \(November 2014\)](#) of Wan Chai Development Phase II (WDII) the key works in [December 2014](#) are as follows:

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

- Nil

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East

- Works of covered walkway
- Drainage works
- ABWF works
- Demolition of the existing Wan Chai Ferry Pier
- Dredging and Reclamation at WCR3

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

- Removal of D-wall at TPCWAE & TS4
- Temporary reclamation and installation of seawall blocks at TPCWAW
- Maintenance dredging
- Reinstatement of existing bermstone and seawall at TS4

Contract no. HY/2009/19- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- Construction of Dolphin Cap
- Construction of Pile Cap F1B

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

- ELS for box culvert L at Lung King Street
- Removal of rock armour
- Dry dock construction
- Installation of caisson seawall

---

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8)

- Rock filling works
- Dredging works
- Seawall block installation
- Sheet piling works, welding & struts installation works at Outfall Q
- Seawater intake diversion works
- Installation of water tank

7.0.3. From the [Monthly EM&A report \(November 2014\)](#) of Central-Wan Chai Bypass (CWB) the key works in [December 2014](#) are as follows:

Contract no. HY/2009/18 - Central - Wan Chai Bypass (CWB) - Central Interchange under FEP-05/364/2009/A

- Excavation of trial pit
- Transplanting of trees
- Drainage works
- Tunnel works including scaffolding erection, excavation, OHVD installation, roadside barriers, top and base slab construction, extract sheet pile, waterproofing and backfill
- Trough structure construction and associated drilling and grouting
- Road works
- Bridges construction

Contract no. HK/2009/01 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Hong Kong Convention and Exhibition Centre - Tunnel Works under FEP-02/364/2009

- Stage 1 construction of tunnel structures would be completed in early Dec 2014
- Stage 2 construction of tunnel structures would be commenced
- Stage 2 ELS works for exhaust duct would be continued and to be completed in mid-Dec 2014
- Stage 3 Excavation and ELS works would be carried out
- The precast unit of Bay 1 would be installed.
- The structure works of Bay 2 and Bay 7 would be in progress at both south and north side of the water channel concurrently.
- Pipelaying works for S5A and S5B would be carried out after plant demobilization at box culvert Bay 2.
- The pipelaying works for discharge cooling main would be continued.
- Pressure test for salt watermain S8B and swabbing works for salt watermain S9 would be carried out.
- Sewage works at Fenwick Pier Street would be carried out

Contract no. HK/2009/02 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

- Excavation & installation of ELS at Strut S3 level
- Excavation & installation of ELS at Strut S4 level
- Bored pile construction
- D-Wall construction works

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- Mined Tunnel drill-and-break works at East and West Portal
- Permanent lining structure at Mined Tunnel

Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/A

- Bored piling (Land)
- ELS for Cut & Cover Tunnel and EVB
- Laying of 1350 pipe
- Pre-bored H-pile for Admin. Building continue
- Construction of Bridge E
- Construction of Bridge F4 and F5 Wing Extension
- Construction of Pump Sump E
- Installation of Noise Barrier/enclosure
- Modification of existing crosshead at Pier 17-18
- IECL Road modification and removal of Median Barrier
- Construction of TB Bridge
- Construction of Pile Cap F1B
- Abutment D12 construction
- Demolition of Hing Fat Street Road

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West under FEP-09/364/2009B

- Diaphragm wall construction
- Bored Pile Construction

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8) under FEP-10/364/2009B

- Tree works within off-site nursery compound
- Drainage improvement works
- Sheet piling works
- Excavation and Lateral Support for U-structure,
- Erection of noise absorption sheetings
- Pipe piling and grouting works,
- Utility diversion,
- Construction of Bowling Green Office and



- Waterproofing works

Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009B

- Construct slab and wall for West Ventilation Building

7.0.4. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activities under Wan Chai Development Phase II were marine works at HKCEC areas, tunnel works and Wan Chai Ferry Pier demolition works at Wan Chai East and dredging works at Wan Chai West. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were bridge construction and road works at Central Interchange, land base bored pilling works at Victoria Park Road and ELS works at Victoria Park, segment launching works and tunnel works at North Point area. Marine-based construction activities were removal of temporary reclamation at TS4 and seawall construction EX-PCWA and seawall construction and filling works at TS3 at Causeway Bay Typhoon Shelter in the reporting month.



---

## **8 Environmental Site Audit**

8.0.1. During this reporting period, weekly environmental site audits were conducted for the SCL Protection Works under the Contract no. HY/2009/15. No non-conformance was identified during the site audits.

**8.0.2.** Four site inspections for Contract no. HY/2009/15 was carried out on 2, 9, 16 and 23 December 2014 in the reporting period. No observation was found during the reporting month period.



## 9 COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION

9.0.1. There was no environmental complaint and prosecution recorded in the reporting period.

9.0.2. The details of cumulative complaint log and updated summary of complaints are presented in **Appendix 7.1**

9.0.3. Cumulative statistic on complaints and successful prosecutions are summarized in **Table 9.1** and **Table 9.2** respectively.

**Table 9.1 Cumulative Statistics on Complaints**

Reporting Period	No. of Complaints
December 2014	0
November 2011 to November 2014	0
Total	0

**Table 9.2 Cumulative Statistics on Successful Prosecutions**

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this period (Offence Date)	Cumulative No. Project-to-Date
Air	-	0	0
Noise	-	0	0
Water	-	0	0
Waste	-	0	0
<b>Total</b>	-	<b>0</b>	<b>0</b>

## 10. CONCLUSION

10.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alternations to the programme proposed were made in response to changing circumstances.

10.0.2. The scheduled construction activities and the recommended mitigation measures for the coming month are listed in **Table 10.1**. The construction programmes of individual contracts are provided in **Appendix 10.1**.

**Table 10.1 Summary of Key Construction Activities of Individual Contract(s) to be commenced in Coming Reporting Month**

Contract No.	Key Construction Works	Recommended Mitigation Measures
HY/2009/15	<ul style="list-style-type: none"> <li>• Installation of seawall blocks and backfilling works for formation of TZ4</li> <li>• Jetty beams construction for permanent RHKYC jetty</li> <li>• Reinstatement of existing bermstone and seawall</li> <li>• Post tunnel construction works at ME4</li> </ul>	<ul style="list-style-type: none"> <li>• Watering for any dust or exposed surface</li> <li>• Daily visual inspection of silt screen and silt curtain to ensure its operation properly</li> <li>• Implement silt curtain in accordance with associated plans submitted to EPD</li> </ul>




**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

***Figure 2.1***

***Project Layout***

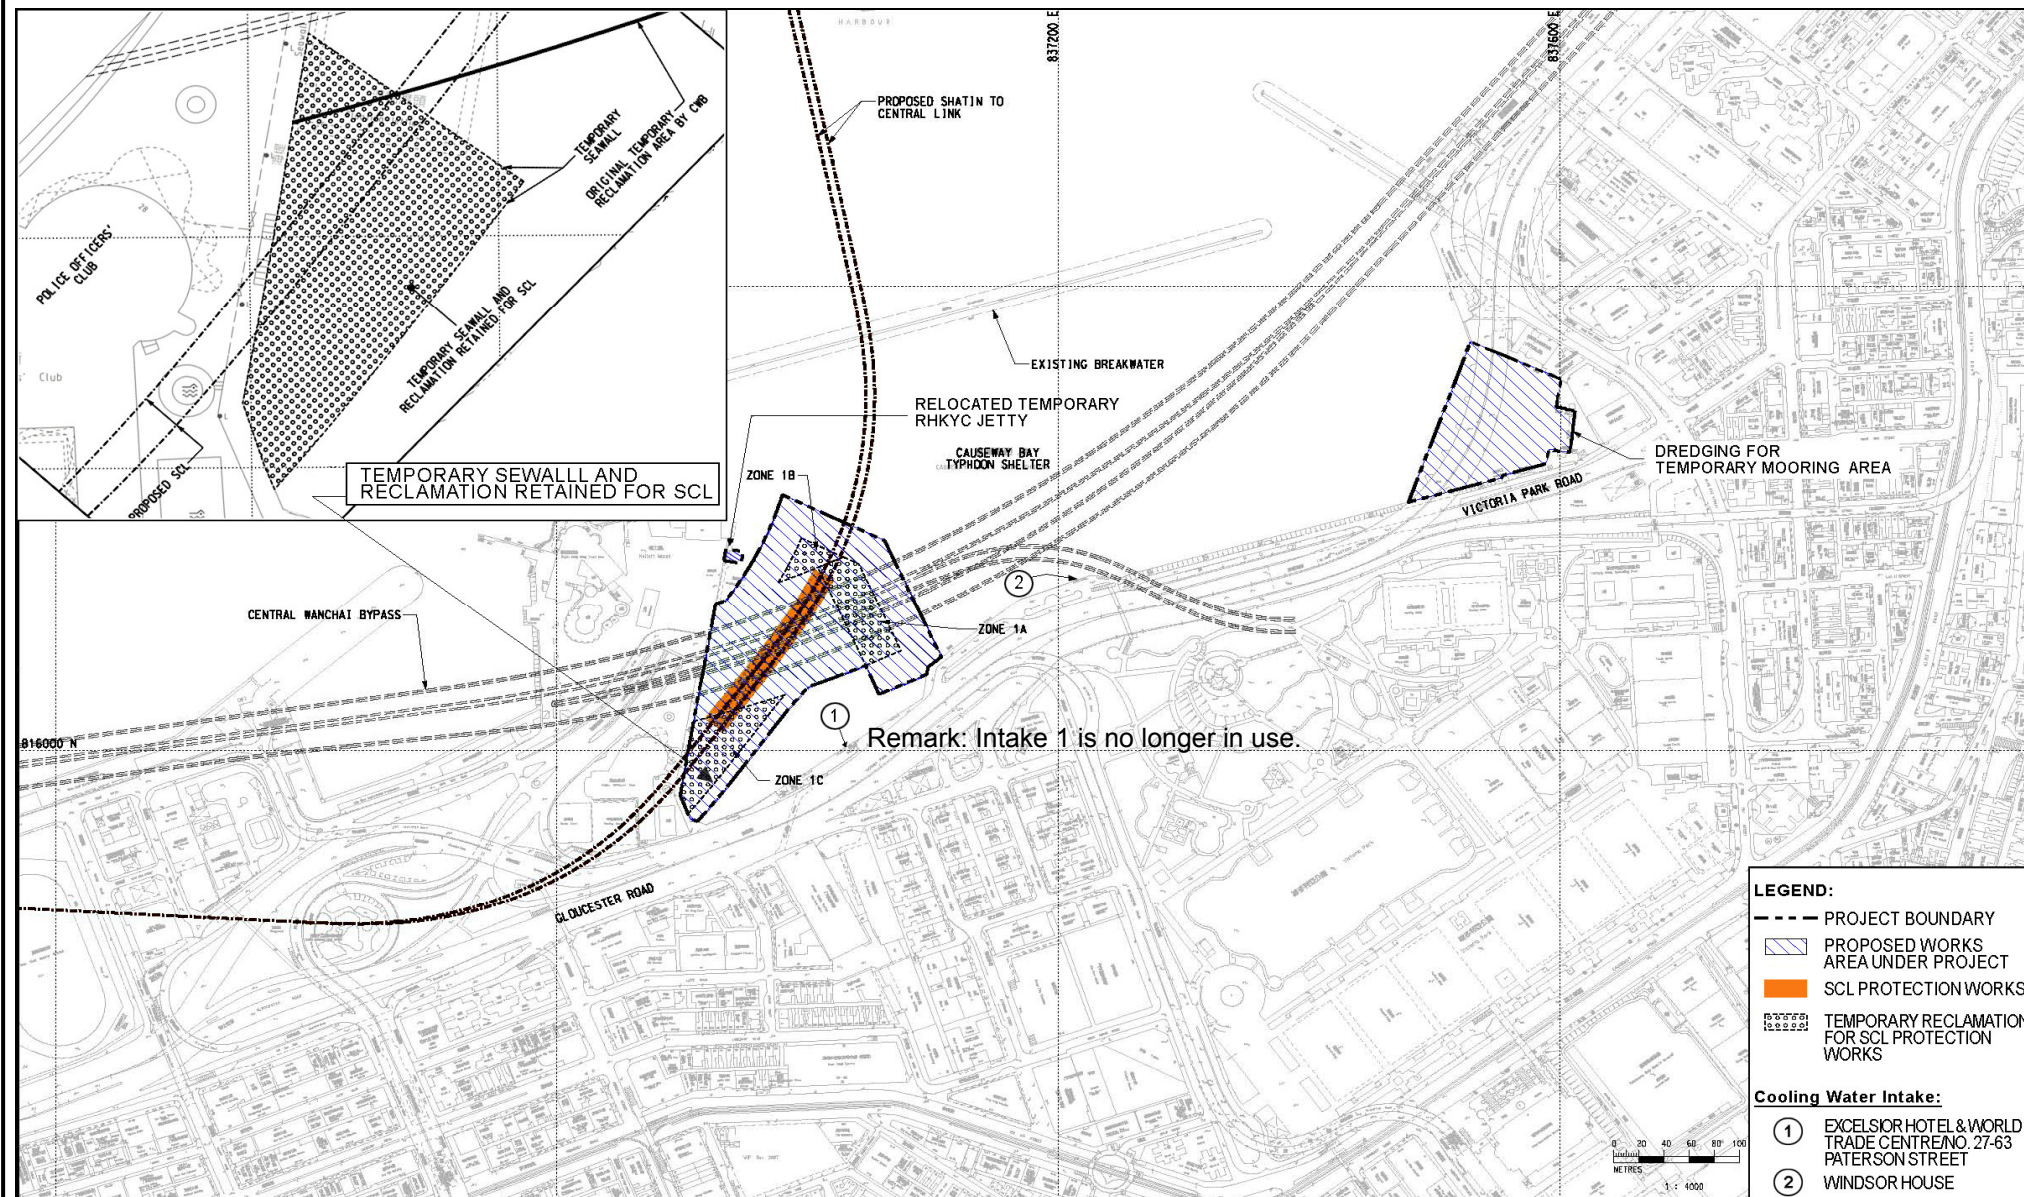



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)


---

***Figure 2.2***

***Project Organization Chart***



**Project Organization Chart**

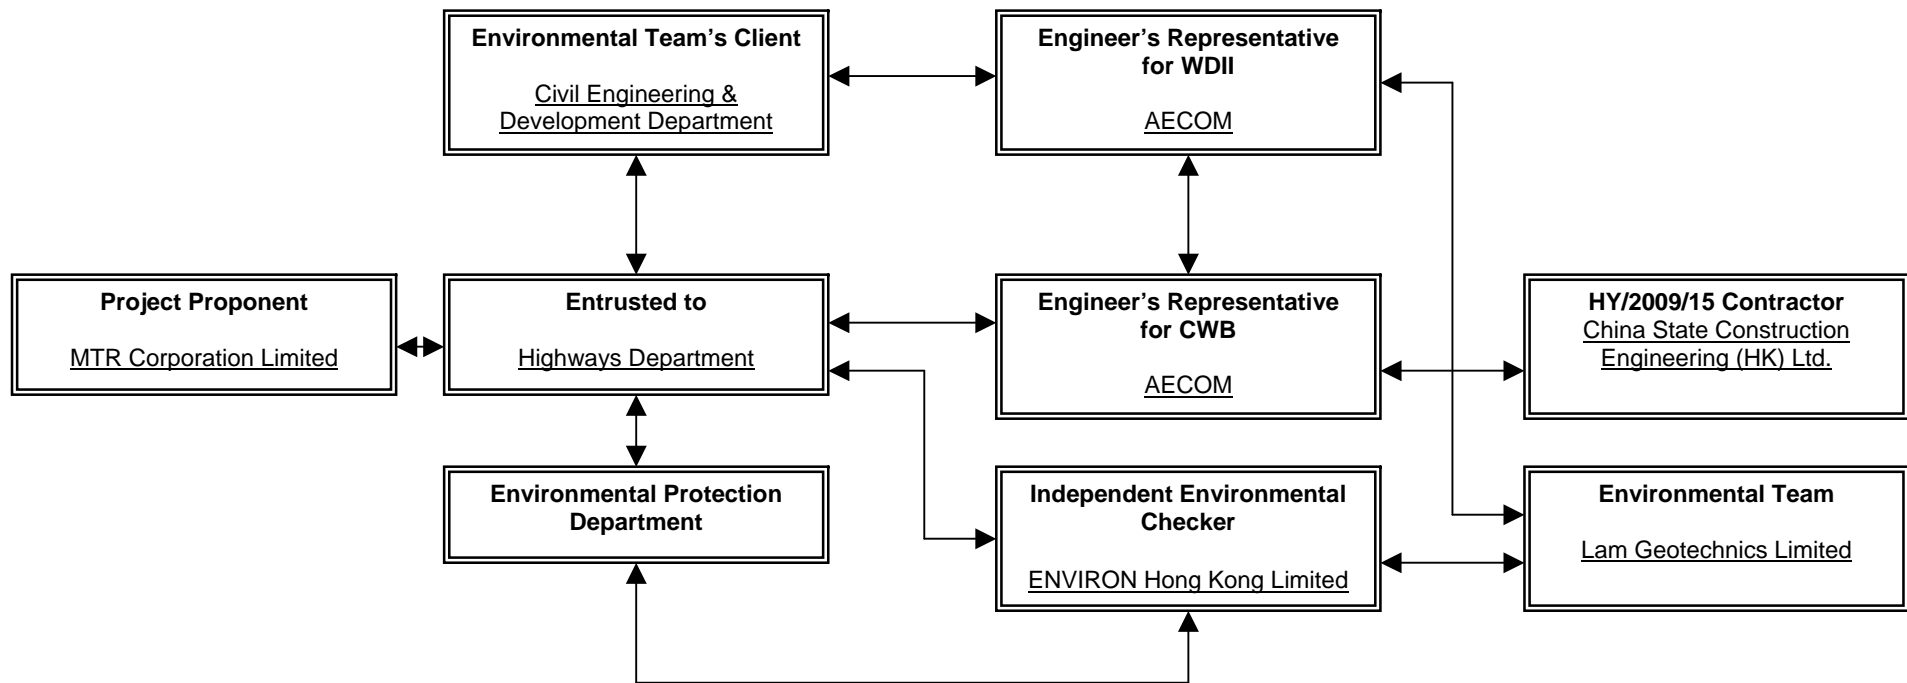



**Lam Geotechnics Limited**


Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

***Figure 2.3***

***Locations of Monitoring Stations***



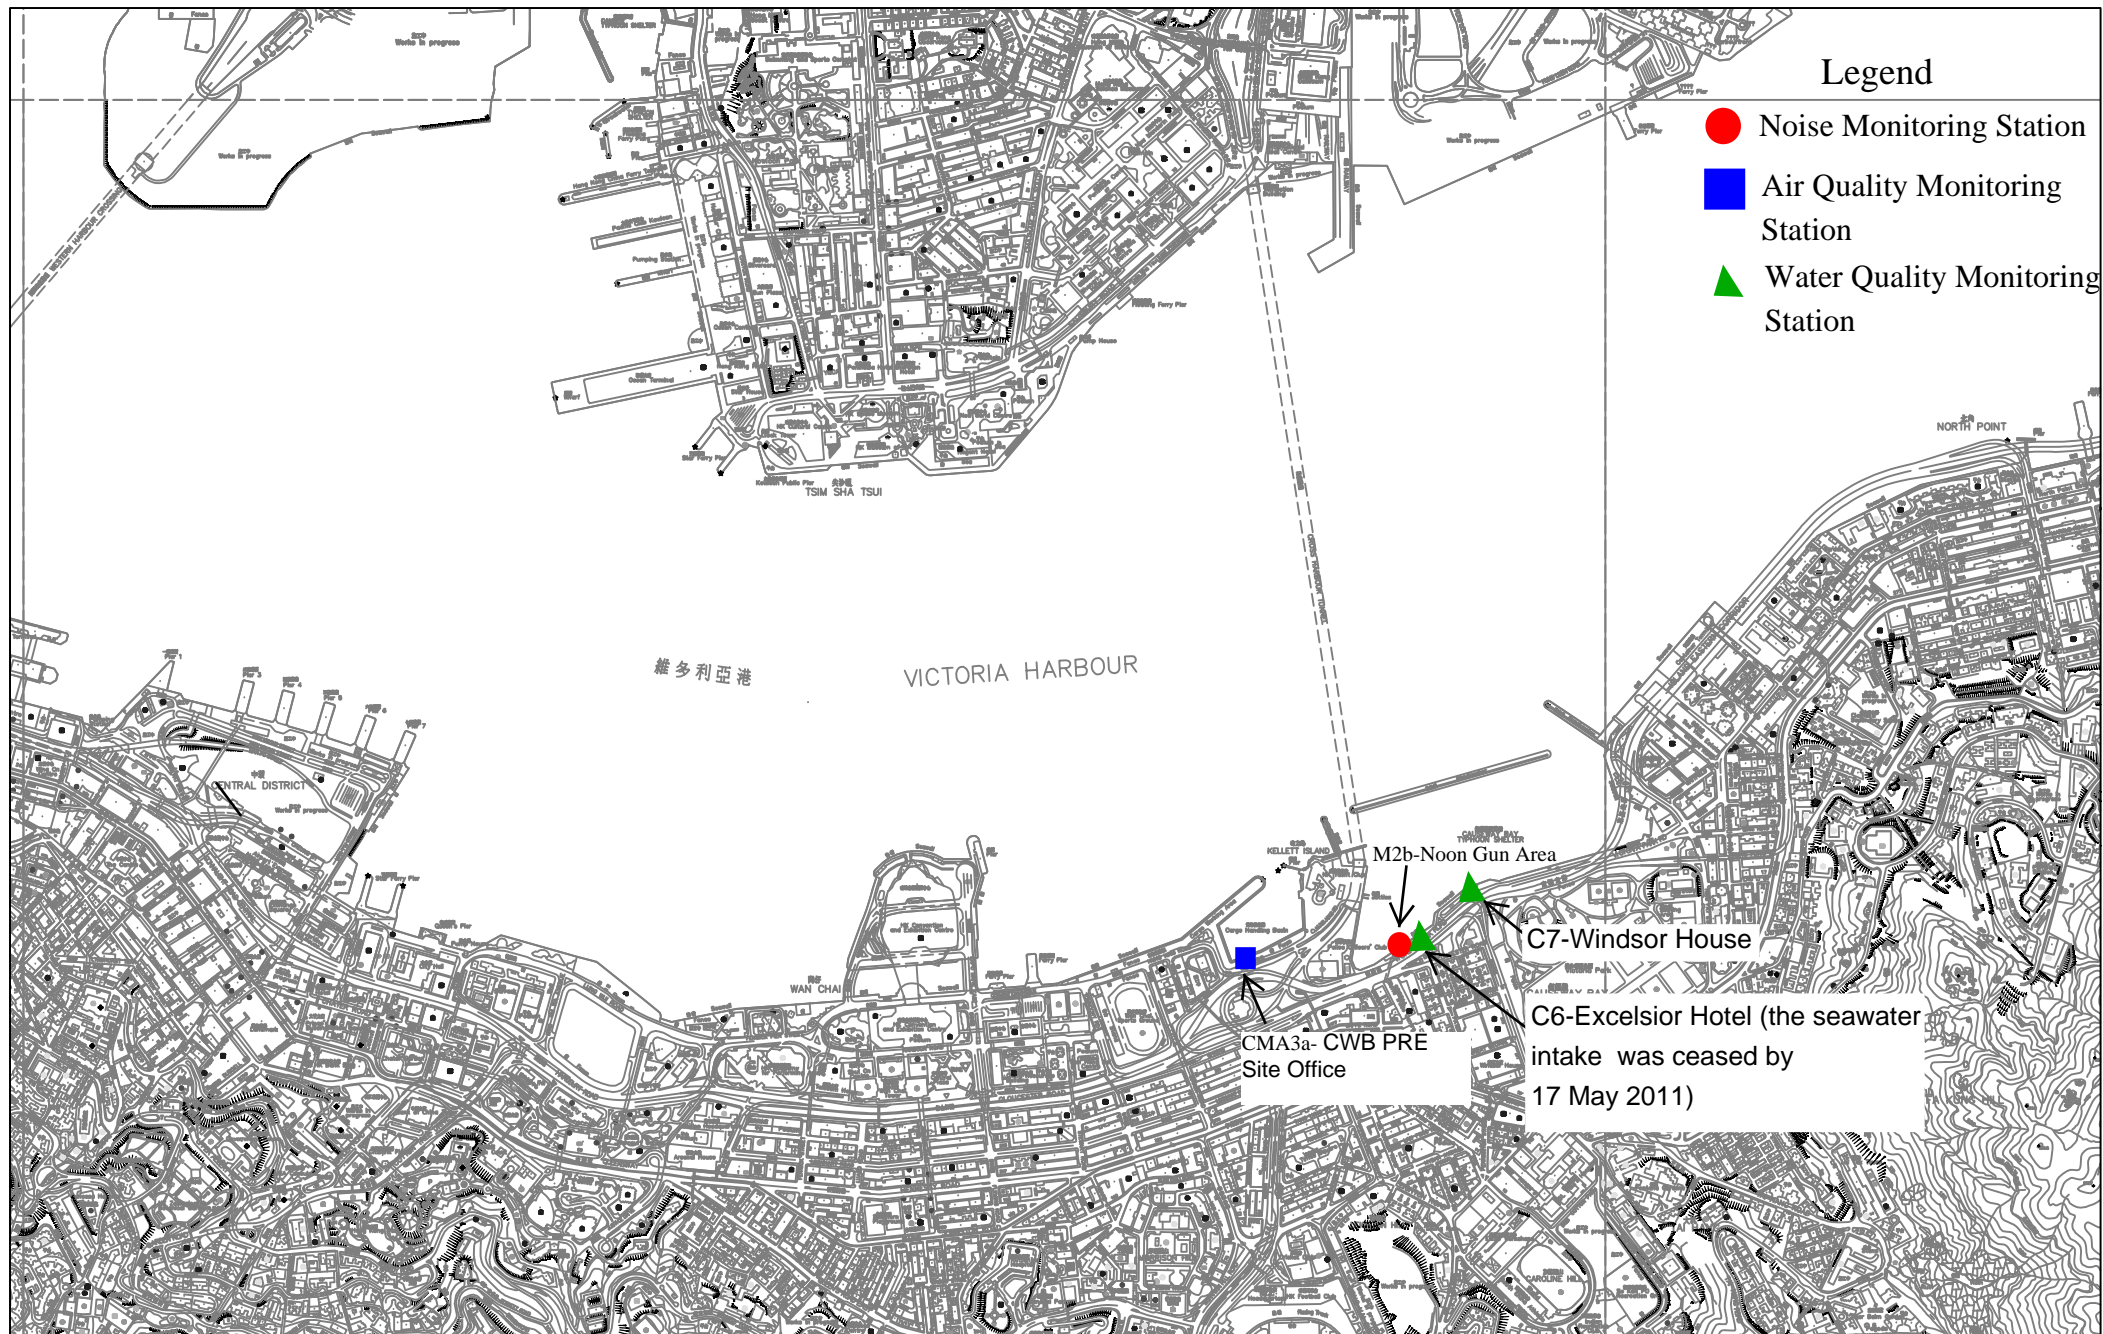





**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

### ***Appendix 3.1***

#### ***Environmental Mitigation Implementation Schedule***

**IMPLEMENTATION SCHEDULE OF THE PROPOSED MITIGATION MEASURES**

<b>EIA Ref.</b>	<b>Recommended Mitigation Measures</b>	<b>Objectives of the Recommended Measures &amp; Main Concern to Address</b>	<b>Who to implement the measures?</b>	<b>Location of the measure</b>	<b>When to implement the measures?</b>	<b>What requirements or standards for the measure to achieve?</b>
<b>Water Quality Impact (Construction Phase)</b>						
3.142	Dredging should be carried out by closed grab dredger.	To minimize release of sediment and contaminants during dredging.	Contractor	Dredging works areas in Causeway Bay Typhoon Shelter (CBTS)	Construction Phase	EIAO-TM, WPCO
S3.142	All temporary reclamation works should adopt an approach where temporary seawalls will first be formed to enclose each phase of the temporary reclamation. Installation of diaphragm wall on temporary reclamation as well as any bulk filling will proceed behind the completed seawall. Any gaps that may need to be provided for marine access should be shielded by silt curtains to control sediment plume dispersion away from the site. Demolition of temporary reclamation including the demolition of the diaphragm wall and dredging to the existing seabed levels	To minimize loss of fines and contaminants during temporary reclamations	Contractor	Temporary reclamation works areas in CBTS	Construction Phase	EIAO-TM, WPCO

	should be carried out behind the temporary seawall. Temporary seawall should be removed after completion of all excavation and dredging works for demolition of the temporary reclamation.					
S3.142	During construction of the temporary reclamation, temporary seawall should be partially constructed to protect the nearby seawater intakes from further dredging activities. For example, the seawalls along the southeast and northeast boundaries of PW1.1 should be constructed first (above high water mark) so that the seawater intake at the inner water would be protected from the impacts from the remaining dredging activities along the northwest boundary.	To minimize water quality impact upon the cooling water intakes in CBTS from temporary reclamation works	Contractor	Temporary reclamation works areas in CBTS	Construction Phase	EIAO-TM, WPCO
S3.142	Silt curtains should be deployed to fully enclose the closed grab dredger during any dredging operation within the CBTS.	To minimize loss of fines and contaminants during dredging in CBTS	Contractor	Dredging works areas in CBTS	Construction Phase	EIAO-TM, WPCO
S3.142	Silt screens will be installed at all the cooling water intakes within the CBTS during temporary reclamation and dredging within the typhoon shelter.	To minimize water quality impact upon the cooling water intakes in CBTS from marine construction activities	Contractor	Cooling water intakes inside CBTS	Construction Phase	EIAO-TM, WPCO
S3.143	No more than two closed grab dredgers should be operated for dredging within the CBTS at	To minimize loss of fines and contaminants	Contractor	Temporary reclamation and	Construction Phase	EIAO-TM, WPCO

	any time. Moreover, the combined production rate of all concurrent dredging works to be undertaken within the CBTS shall not exceed 6,000 m <sup>3</sup> per day at all times throughout the entire construction period.	during dredging in CBTS		dredging works areas in CBTS		
S3.145	<p>The following good site practices should be undertaken during sand filling, public filling and dredging:</p> <ul style="list-style-type: none"> <li>• mechanical grabs, if used, should be designed and maintained to avoid spillage and sealed tightly while being lifted. For dredging of any contaminated mud, closed watertight grabs must be used;</li> <li>• all vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash;</li> <li>• all hopper barges and dredgers should be fitted with tight fitting seals to their bottom openings to prevent leakage of material;</li> <li>• construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the</li> </ul>	To minimize loss of fines and contaminants from dredging / filling	Contractor	Temporary reclamation and dredging works areas in CBTS	Construction Phase	EIAO-TM, WPCO

	site or dumping grounds; and <ul style="list-style-type: none"> <li>loading of barges and hoppers should be controlled to prevent splashing of dredged material into the surrounding water. Barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation.</li> </ul>					
S3.146	The following mitigation measures are proposed to minimize the potential water quality impacts from the construction works at or close to the seafront: <ul style="list-style-type: none"> <li>Temporary storage of construction materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction and demolition materials should be located well away from the seawater front and storm drainage during carrying out of the works.</li> <li>Stockpiling of construction and demolition materials and dusty materials should be covered and located away from the seawater front and storm drainage.</li> <li>Construction debris and spoil should be covered up and/or disposed of as soon as</li> </ul>	To minimize release of construction wastes from construction works at or close to the seafront	Contractor	Construction works at or close to the seafront	Construction Phase	EIAO-TM, WPCO

	possible to avoid being washed into the nearby receiving waters.					
S3.147	Silt curtains should be installed around the working area for the marine piling works for construction of the temporary jetty as necessary to minimize the release of sediment and construction wastes. All wastewater generated from the piling activities should be collected by a derrick lighter or other collection system and be treated before controlled discharge. Spoil from the piling activities should be collected by sealed hopper barges for proper disposal.	To minimize water quality impacts from piling works for construction of the temporary jetty	Contractor	Piling area at the piling location	Construction Phase	EIAO-TM, WPCO
S3.148	Regular maintenance of and refuse collection should be performed at the silt screens deployed at the seawater intakes at regular intervals on a daily basis. The Contractor should be responsible for keeping the water behind the silt screen free from floating rubbish and debris during the impact monitoring period.	To avoid the pollutant and refuse entrapment problems at the silt screens to be installed at the water intakes	Contractor	Proposed silt screens at cooling water intakes inside CBTS	Construction Phase	EIAO-TM, WPCO
S3.149	It is recommended that collection and removal of floating refuse should be performed within the marine construction areas at regular intervals on a daily basis. The Contractor should be	To minimize water quality impacts from illegal dumping and littering from marine vessels and runoff from	Contractor	All marine works areas	Construction Phase	EIAO-TM, WPCO, WDO

	responsible for keeping the water within the site boundary and the neighbouring water free from rubbish during the dredging works.	the coastal areas				
S3.150 to 3.169	The site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" should be followed where practicable.	To minimize water quality impacts from construction site runoff and general construction activities	Contractor	All construction works areas	Construction Phase	EIAO-TM, WPCO, TM-DSS, WDO, ProPECC PN 1/94
S3.170	There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. Minimum distances of 100 m should be maintained between the discharge points of construction site effluent and the existing seawater intakes. The beneficial uses of the treated effluent for other on-site activities such as dust suppression, wheel washing and general cleaning etc., can minimise water consumption	To minimize water quality impact from effluent discharges from construction sites	Contractor	All construction works areas	Construction Phase	EIAO-TM, WPCO, TM-DSS

	and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of Regional Office (RO) of EPD.					
S3.171 & 3.172	Construction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. If disposal of sewage to public sewerage system is not feasible, appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the construction workers over the construction site to prevent direct disposal of sewage into the water environment. The Contractor shall also be responsible for waste disposal and maintenance practices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment.	To minimize water quality impacts due to sewage generated from construction workforce	Contractor	All construction works areas	Construction Phase	EIAO-TM, WPCO, TM-DSS, WDO
S3.173	Contractor must register as a chemical waste producer if	To minimize water quality	Contractor	All construction	Construction Phase	EIAO-TM, WPCO, TM-



	chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	impact from accidental spillage of chemical		works areas		DSS, WDO
S3.174	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	To minimize water quality impact from accidental spillage of chemical	Contractor	All construction works areas	Construction Phase	EIAO-TM, WPCO, TM-DSS, WDO
S3.175	Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The "Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes" published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows: <ul style="list-style-type: none"> <li>Suitable containers should</li> </ul>	To minimize water quality impact from accidental spillage of chemical	Contractor	All construction works areas	Construction Phase	EIAO-TM, WPCO, TM-DSS, WDO

	<p>be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</p> <ul style="list-style-type: none"> <li>• Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents.</li> <li>• Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.</li> </ul>					
S4. 30	<p>The following good site practices should be implemented:</p> <ul style="list-style-type: none"> <li>• Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program</li> <li>• Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program</li> <li>• Mobile plant, if any, should be sited as far from NSRs as possible</li> <li>• Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum</li> </ul>	To reduce construction noise impact	Contractor	All works areas	Construction phase	EIAO-TM, NCO

	<ul style="list-style-type: none"> <li>Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs</li> <li>Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities.</li> </ul>					
S4.31 – S4.32 & Table 4.7	<p>The following quiet PME are recommended for the construction activities:</p> <p>Air Compressor Bulldozer Concrete Pump Concrete Lorry Mixer Crane Dump Truck Excavator Generator Hand-held Breaker Poker Vibrator Roller Trucks</p>	To reduce construction noise impact	Contractor	All works areas	Construction phase	EIAO-TM, NCO
S4.33 – S4.35 & Table 4.8	<p>Movable noise barrier should be used for the following PME:</p> <p>Air Compressor Bar Bender Bentonite Plants Concrete pump Diaphragm Wall Rigs Excavator</p>	To reduce construction noise impact	Contractor	Affected works areas showing exceedance during un-mitigated scenario	Construction phase	EIAO-TM, NCO

	Poker Vibrator					
<b>Construction Dust Impact</b>						
S5.43	Watering once on construction areas for every working hour	To minimize dust impact	Contractor	Temporary reclamation area in CBTS	Construction phase	APCO
S5.43	Covering/paving the southwest retained area of temporary reclamation once filling is completed	To minimize dust impact	Contractor	southwest retained area of temporary reclamation	Construction phase	phase APCO
S5.44	<p>Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices:</p> <p>Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather.</p> <p>Use of frequent watering for particularly dusty construction areas and areas close to ASRs.</p> <p>Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.</p>	To minimize dust impacts	Contractor	Temporary reclamation area in CBTS	Construction phase	APCO and Air Pollution Control (Construction Dust) Regulation

	<p>Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs.</p> <p>Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.</p> <p>Establishment and use of vehicle wheel and body washing facilities at the exit points of the site.</p> <p>Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods.</p> <p>Provision of not less than 2.4m high hoarding from ground level along site boundary where adjoins a road, streets or other accessible to the public except for a site entrance or exit.</p> <p>Imposition of speed controls for vehicles on site haul roads.</p> <p>Where possible, routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs.</p>					
--	---	--	--	--	--	--

	<p>Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.</p> <ul style="list-style-type: none"> <li>• Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.</li> </ul>					
<b>Waste Management implications (Construction Phase)</b>						
6.62	<p><b>Good Site Practices and Waste Reduction Measures</b></p> <ul style="list-style-type: none"> <li>- Prepare a Waste Management Plan approved by the Engineer/Supervising Officer of the Project based on current practices on construction sites;</li> <li>- Training of site personnel in, site cleanliness, proper waste management and chemical handling procedures;</li> <li>- Provision of sufficient waste disposal points and regular collection of waste;</li> <li>- Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;</li> <li>- Regular cleaning and</li> </ul>	To enhance water management practice and achieve waste reduction.	Contractor	All Work Sites	Construction Phase	Waste Disposal Ordinance (Cap. 354) Land (Miscellaneous Provisions) Ordinance (Cap. 28) ETWB TC(W) No.31/2004

	<p>maintenance programme for drainage systems, sumps and oil interceptors; and</p> <ul style="list-style-type: none"> <li>- Separation of chemical wastes for special handling and appropriate treatment.</li> </ul>					
6.63	<p><b>Good Site Practices and Waste Reduction Measures (con't)</b></p> <ul style="list-style-type: none"> <li>- Sorting of demolition debris and excavated materials from demolition works to recover reusable/ recyclable portions (i.e. soil, broken concrete, metal etc.);</li> <li>- Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>- Encourage collection of aluminum cans by providing separate labeled bins to enable this waste to be segregated from other general refuse generated by the workforce;</li> <li>- Proper storage and site practices to minimize the potential for damage or contamination of construction materials;</li> <li>- Plan and stock construction</li> </ul>	To achieve waste reduction	Contractor	All Work Sites	Construction Phase	<p>Waste Disposal Ordinance (Cap. 354)</p> <p>Land (Miscellaneous Provisions) Ordinance (Cap. 28)</p>

	materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste; and - Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycle.					
6.64	<b><i>Good Site Practices and Waste Reduction Measures (con't)</i></b> - The Contractor shall prepare and implement an EMP in accordance with ETWB TCW No. 19/2005. Such management plan should incorporate site specific factors, such as the designation of areas for segregation and temporary storage of reusable and recyclable materials. The EMP should be submitted to the Engineer for approval. The Contractor should implement the waste management practices in the EMP throughout the construction stage of the Project. The EMP should be reviewed regularly and updated by the Contractor, preferably in a monthly basis.	To enhance water management practice and achieve waste reduction.	Contractor	All Work Sites	Construction Phase	ETWB TCW No. 19/2005



6.66	<b><i>Storage, Collection and Transportation of Waste</i></b> - Waste, such as soil, should be handled and stored well to ensure secure containment, thus minimizing the potential of pollution; - Maintain and clean storage areas routinely; - Stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; and - Different locations should be designated to stockpile each material to enhance reuse.	To minimize potential adverse environmental impacts arising from waste storage	Contractor	Work Sites	Construction Phase	-
6.67	<b><i>Storage, Collection and Transportation of Waste (con't)</i></b> - Waste haulier with appropriate permits should be employed by the Contractor for the collection and transportation of waste from works areas to respective disposal outlets.	To minimize potential adverse environmental impacts arising from waste collection and disposal	Contractor	Waste storage area.	Construction Phase	-
6.68	<b><i>Storage, Collection and Transportation of Waste (con't)</i></b> - Implementation of trip ticket system with reference to ETWB TC(W) No.31/2004 to monitor disposal of waste and to control fly-tipping at PFRFs or landfills.	To minimize potential adverse environmental impacts arising from waste collection and disposal	Contractor	Work Sites	Construction Phase	ETWB TC(W) No.31/2004

	A recording system for the amount of waste generated, recycled and disposed (including disposal sites) should be proposed.					
6.70 – 6.73	<b>Sorting of C&amp;D Materials</b> <ul style="list-style-type: none"> <li>- Sorting to be performed to recover the inert materials, reusable and recyclable materials before disposal off-site.</li> <li>- Specific areas should be provided by the Contractors for sorting and to provide temporary storage areas for the sorted materials.</li> <li>- The C&amp;D materials should at least be segregated into inert and non-inert materials, in which the inert portion could be reused and recycled as far as practicable before delivery to PFRFs as mentioned for beneficial use in other projects. While opportunities for reusing the non-inert portion should be investigated before disposal of at designated landfills.</li> <li>- Possibility of reusing the spoil in the Project will be continuously investigated in the construction stage.</li> </ul>	To minimize potential adverse environmental impacts during the handling, transportation and disposal of C&D materials	Contractor	All work Sites	Construction Phase	ETWB TCW No. 31/2004 ETWB TCW No. 33/2002 ETWB TCW No. 19/2005
6.75	<b>Sediments</b> <ul style="list-style-type: none"> <li>- The basic requirements and procedures for dredged</li> </ul>	To ensure the sediment to be disposed of in an	Contractor	All works areas with sediments	Construction Phase	PNAP 252

	sediment disposal specified under PNAP 252 shall be followed. MFC manages disposal facilities in Hong Kong for the dredged sediment, while EPD is the authority issuing marine dumping permits under the <i>Dumping at Sea Ordinance</i> .	authorized and least impacted way		concern		
6.76	<b>Sediments (con't)</b> - The Project Proponent should agree in advance with MFC of CEDD on the site allocation by submitting a Construction & Demolition Material Management Plan. The contractor for the dredging works shall then apply for the site allocations of marine sediment disposal based on the prior agreement with MFC/CEDD. A request for reservation of sediment disposal space has been submitted to MFC for onward discussions of disposal approaches and feasible disposal sites. The Project Proponent is also responsible for application of all necessary permits from the relevant authorities, including the dumping permit as required under DASO from EPD, for the disposal of dredged sediment prior to the commencement of the dredging works.	To determine the best handling and disposal option of the sediments	MTR / Contractor	All works areas with sediments concern	Prior to the start of dredging works	PNAP 252; Dumping at Sea Ordinance

6.77 – 6.81	<p><b><i>Sediments (con't)</i></b></p> <ul style="list-style-type: none"> <li>- Requirements of the Air Pollution Ordinance (Construction Dust) Regulation, where relevant, shall be adhered to during dredging, transportation and disposal of sediments.</li> <li>- Stockpiling of contaminated sediments should be avoided as far as possible. If temporary stockpiling of contaminated sediments is necessary, the dredged sediment should be covered by tarpaulin and the area should be placed within earth bunds or sand bags to prevent leachate from entering the ground, nearby drains and/or surrounding water bodies. The stockpiling areas should be completely paved or covered by linings in order to avoid contamination to underlying soil or groundwater. Separate and clearly defined areas should be provided for stockpiling of contaminated and uncontaminated materials. Leachate, if any, should be collected and discharged according to the Water Pollution Control Ordinance (WPCO).</li> <li>- In order to minimise the potential odour / dust emissions during dredging and</li> </ul>	To ensure handling of sediments are in accordance to statutory requirements	Contractor	Work Sites, Sediment disposal sites	Construction Phase	PNAP 252 Dumping at Sea Ordinance
----------------	---	---	------------	-------------------------------------	--------------------	-----------------------------------

	<p>transportation of the sediment, the dredged sediments should be properly covered when placed on barges. Loading of the dredged sediment to the barge should be controlled to avoid splashing and overflowing of the sediment slurry to the surrounding water.</p> <ul style="list-style-type: none"> <li>- The barge transporting the sediments to the designated disposal sites should be equipped with tight fitting seals to prevent leakage and should not be filled to a level that would cause overflow of materials or laden water during loading or transportation. In addition, monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the DEP.</li> <li>- In order to minimise the exposure to contaminated materials, workers should wear appropriate personal protective equipments (PPE) when handling contaminated sediments. Adequate washing and cleaning facilities should also be provided on site.</li> </ul>					
--	---	--	--	--	--	--

6.82	<b><i>Sediments (con't)</i></b> The dredging work and associate sediment handling under this Project will be undertaken together with the CWB project by Highways Department and geosynthetic containment will be adopted to handle Type 3 sediments.	To ensure handling of sediments are in accordance to statutory requirements	Contractor	Work Sites, Sediment disposal sites	Construction Phase	PNAP 252 Dumping at Sea Ordinance
6.86	<b><i>Containers for Storage of Chemical Waste</i></b> The Contractor should register with EPD as a chemical waste producer and to follow the guidelines stated in the <i>Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes</i> . Containers used for storage of chemical waste should: <ul style="list-style-type: none"> <li>- Be compatible with the chemical wastes being stored, maintained in good condition and securely sealed;</li> <li>- Have a capacity of less than 450 liters unless the specifications have been approved by EPD; and</li> </ul>	To register with EPD as a Chemical waste producer and store chemical waste in appropriate containers	Contractor	Chemical waste storage area	Construction Phase	Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes

	- Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Waste Disposal (Chemical Waste) (General) Regulation.					
6.87	<b>Chemical Waste Storage Area</b> - Be clearly labeled to indicate corresponding chemical characteristics of the chemical waste and used for storage of chemical waste only; - Be enclosed on at least 3 sides; - Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; - Have adequate ventilation; - Be covered to prevent rainfall from entering; and - Be properly arranged so that incompatible materials are adequately separated.	To prepare appropriate storage areas for chemical waste at works areas	Contractor	Chemical waste storage area	Construction Phase	Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
6.88	<b>Labelling of Chemical Waste</b> - Lubricants, waste oils and other chemical wastes would be generated during the maintenance of vehicles and mechanical equipments. Used	To clearly label the chemical waste at works areas	Contractor	Chemical waste storage area	Construction Phase	Code of Practice on the Packaging, Labelling and Storage of Chemical

	lubricants should be collected and stored in individual containers which are fully labeled in English and Chinese and stored in a designated secure place.					Wastes
6.89	<b><i>Collection and Disposal of Chemical Waste</i></b> - A trip-ticket system should be operated in accordance with the <i>Waste Disposal (Chemical Waste) (General) Regulation</i> to monitor all movements of chemical waste. The Contractor shall employ a licensed collector to transport and dispose of the chemical wastes, to either the approved CWTC at Tsing Yi, or another licensed facility, in accordance with the <i>Waste Disposal (Chemical Waste) (General) Regulation</i> .	To monitor the generation, reuse and disposal of chemical waste	Contractor	Work Sites with chemical waste production	Construction Phase	Waste Disposal (Chemical Waste) (General) Regulation
6.90	<b><i>General Refuse</i></b> - General refuse should be stored in enclosed bins or compaction units separate from C&D materials and chemical waste. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D materials and chemical wastes. Preferably, an enclosed and	To properly store and separate from other C&D materials for subsequent collection and disposal	Contractor	All Work Sites	Construction Phase	-



	covered area should be provided to reduce the occurrence of windblown light material.					
6.91	<b>General Refuse (con't)</b> - The recyclable component of general refuse, such as aluminum cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.	To facilitate recycling of recyclable portions of refuse	Contractor	All Work Sites	Construction Phase	-
6.92	<b>General Refuse (con't)</b> - The Contractor should carry out an education programme for workers in avoiding, reducing, reusing and recycling of materials generation. Posters and leaflets advising on the use of the bins should also be provided in the sites as reminders.	To raise workers' awareness on recycling issue	Contractor	All Work Sites	Construction Phase	-



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

## ***Appendix 4.1***

### ***Action and Limit Level***



## **Action and Limit Level**

### *Action and Limit Level for Air Quality Monitoring*

1-hour TSP Level in $\mu\text{g}/\text{m}^3$		24-hour TSP Level in $\mu\text{g}/\text{m}^3$	
Action Level	Limit Level	Action Level	Limit Level
311.3	500	171.0	260

### *Action and Limit Level for Noise Monitoring*

Time Period	Action Level	Limit Level
07:00 – 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A)/ 70 dB(A)/ 65 dB(A) <sup>Note 1</sup>

Note 1:

- 70dB(A) and 65 dB(A) for schools during normal teaching periods and school examination periods, respectively.
- If works are to be carried out during the restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

### *Action and Limit Level for Water Quality Monitoring*

Parameters	Dry Season		Wet Season	
	Action Level	Limit Level	Action Level	Limit Level
<b>Cooling Water Intake</b>				
SS in mg/L	15.00	22.13	18.42	27.54
Turbidity in NTU	9.10	10.25	11.35	12.71
DO in mg/L	3.36	2.73	3.02	2.44

Remarks: - Contractor shall implement additional improvement measures in case of oxygen depletion (i.e. DO level <2 mg/L) detected within CBTS.



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

## ***Appendix 4.2***

### ***Copies of Calibration Certificates***



## CERTIFICATE OF CALIBRATION

Certificate No.: 14CA0529 01-01 Page 1 of 2

### Item tested

Description:	Sound Level Meter (Type 1)	Microphone
Manufacturer:	B & K	B & K
Type/Model No.:	2236	4188
Serial/Equipment No.:	2100736	2157055
Adaptors used:	-	-

### Item submitted by

Customer Name: Lam Geotechnics Limited  
Address of Customer: -  
Request No.: -  
Date of receipt: 29-May-2014

Date of test: 29-May-2014

### Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Multi function sound calibrator	B&K 4226	2288444	22-Jun-2014	CIGISMEC
Signal generator	DS 360	33873	09-Apr-2015	CEPREI
Signal generator	DS 360	61227	09-Apr-2015	CEPREI

### Ambient conditions

Temperature:  $22 \pm 1$  °C  
Relative humidity:  $60 \pm 10$  %  
Air pressure:  $1000 \pm 10$  hPa

### Test specifications

1. The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
2. The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of  $\pm 20\%$ .
3. The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsiveness of the Sound Level Meter.

### Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Approved Signatory:

  
Huang Jian Min / Feng Jun Qi

Date: 30-May-2014

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



## CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 14CA0529 01-01

Page 2 of 2

### 1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertainty (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	2.1
	C	Pass	1.0	
	Lin	Pass	2.0	
Linearity range for Leq	At reference range, Step 5 dB at 4 kHz	Pass	0.3	2.2
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
Linearity range for SPL	A	Pass	0.3	
	C	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	Pass	0.3	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/10 <sup>3</sup> at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 <sup>4</sup> at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

### 2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertainty (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
	Weighting A at 8000 Hz	Pass	0.5	

### 3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

Date:

Fung Chi Yip

29-May-2014

- End -

Checked by:

Date:

Lam Tze Wai

30-May-2014

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.





## CERTIFICATE OF CALIBRATION

Certificate No.: 14CA0529 01-02

Page: 1 of 2

### Item tested

Description: Acoustical Calibrator (Class 1)  
Manufacturer: Rion Co., Ltd.  
Type/Model No.: NC-73  
Serial/Equipment No.: 10465798  
Adaptors used: -

### Item submitted by

Customer: Lam Geotechnics Limited  
Address of Customer: -  
Request No.: -  
Date of receipt: 29-May-2014

Date of test: 30-May-2014

### Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2412857	13-May-2015	SCL
Preamplifier	B&K 2673	2239857	10-Apr-2015	CEPREI
Measuring amplifier	B&K 2610	2346941	08-Apr-2015	CEPREI
Signal generator	DS 360	61227	09-Apr-2015	CEPREI
Digital multi-meter	34401A	US36087050	17-Dec-2014	CEPREI
Audio analyzer	8903B	GB41300350	07-Apr-2015	CEPREI
Universal counter	53132A	MY40003662	11-Apr-2015	CEPREI

### Ambient conditions

Temperature:  $22 \pm 1$  °C  
Relative humidity:  $60 \pm 10$  %  
Air pressure:  $1000 \pm 10$  hPa

### Test specifications

- 1, The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- 2, The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- 3, The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

### Test results

Details of the performed measurements are presented on **page 2** of this certificate.

Approved Signatory:

Huang Jian Min/Feng Jun Qi

Date: 30-May-2014

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



## CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.: 14CA0529 01-02

Page: 2 of 2

### 1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

Frequency Shown Hz	Output Sound Pressure Level Setting dB	Measured Output Sound Pressure Level dB	(Output level in dB re 20 $\mu$ Pa)
			Estimated Expanded Uncertainty dB
1000	94.00	94.57	0.10

### 2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

At 1000 Hz STF = 0.001 dB

Estimated expanded uncertainty 0.005 dB

### 3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz Actual Frequency = 965.6 Hz

Estimated expanded uncertainty 0.1 Hz Coverage factor k = 2.2

### 4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz TND = 0.9 %

Estimated expanded uncertainty 0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

Calibrated by:

Date: 30-May-2014

Fung Chi Yip

- End -

Checked by:

Date: 30-May-2014

Lam Tze Wai

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.



**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION****Information supplied by customer:**

**CONTACT:** DEREK LO **WORK ORDER:** HK1410350  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 2014-11-25  
**DATE OF ISSUE:** 2014-12-02  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** ---

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203010
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	25-Nov-14

**Remarks:**

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

Address: Room 1503, 15/F, Wayson Commercial House, 68-70 Lockhart Road, Wanchai, Hong Kong

Phone +852 2527 6691 | Email info@pilot-testing.com

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1410350  
**DATE OF ISSUE:** 2014-12-02  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203010
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	25-Nov-14
<b>Date of next Calibration:</b>	25-Feb-15

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	3.86	-3.5
10	10.2	2.0
40	39.1	-2.3
100	104	4.0
400	412	3.0
1000	994	-0.6
	<b>Tolerance Limit (±%)</b>	<b>10.0</b>

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION****Information supplied by customer:**

**CONTACT:** DEREK LO **WORK ORDER:** HK1410310  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 9/10/2014  
**DATE OF ISSUE:** 16/10/2014  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** ---

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203008
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	09-Oct-14

**Remarks:**

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1410310  
**DATE OF ISSUE:** 16/10/2014  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203008
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	09-Oct-14
<b>Date of next Calibration:</b>	09-Jan-15

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	4.13	3.3
10	10.3	3.0
40	39.8	-0.5
100	101	1.0
400	380	-5.0
1000	980	-2.0
	Tolerance Limit ( $\pm\%$ )	10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

Address: Room 1503, 15/F, Wayson Commercial House, 68-70 Lockhart Road, Wanchai, Hong Kong  
Phone +852 2527 6691 | Email info@pilot-testing.com



**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION****Information supplied by customer:**

**CONTACT:** DEREK LO **WORK ORDER:** HK1410311  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 9/10/2014  
**DATE OF ISSUE:** 16/10/2014  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** ---

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203015
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	09-Oct-14

**Remarks:**

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1410311  
**DATE OF ISSUE:** 16/10/2014  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203015
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	09-Oct-14
<b>Date of next Calibration:</b>	09-Jan-15

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	3.90	-2.5
10	10.2	2.0
40	39.3	-1.8
100	103	3.0
400	388	-3.0
1000	986	-1.4
Tolerance Limit ( $\pm\%$ )		10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

Address: Room 1503, 15/F, Wayson Commercial House, 68-70 Lockhart Road, Wanchai, Hong Kong  
Phone +852 2527 6691 | Email info@pilot-testing.com



ALS Technichem (HK) Pty Ltd  
11/F, Chung Shun Knitting Centre  
1-3 Wing Yip Street  
Kwai Chung, N.T., Hong Kong  
T: +852 2610 1044  
F: +852 2610 2021  
www.alsglobal.com

## REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

**CONTACT:** MR ALAN LI  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**ADDRESS:** 11/F., CENTRE POINT,  
181-185 GLOUCESTER ROAD,  
WAN CHAI, HONG KONG

**WORK ORDER:** HK1436509  
**LABORATORY:** HONG KONG  
**DATE RECEIVED:** 10/11/2014  
**DATE OF ISSUE:** 17/11/2014

### COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.


The "Next Calibration Date" is recommended according to best practice principals as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.

Scope of Test: Dissolved Oxygen, pH, Salinity and Temperature  
Equipment Type: Multifunctional Meter  
Brand Name: YSI  
Model No.: Professional Plus  
Serial No.: 11F100597  
Equipment No.: --  
Date of Calibration: 17 November, 2014

### NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

  
Mr. Fung Lim Chee, Richard  
General Manager -  
Greater China & Hong Kong



# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order: HK1436509  
Date of Issue: 17/11/2014  
Client: LAM GEOTECHNICS LIMITED



Equipment Type: Multifunctional Meter  
Brand Name: YSI  
Model No.: Professional Plus  
Serial No.: 11F100597  
Equipment No.: --  
Date of Calibration: 17 November, 2014

Date of next Calibration: 17 February, 2015

## Parameters:

### Dissolved Oxygen

Method Ref: APHA (21st edition), 4500O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.60	3.57	-0.03
6.24	6.20	-0.04
8.06	8.03	-0.03
Tolerance Limit (mg/L)		±0.20

### pH Value

Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	4.09	+0.09
7.0	7.19	+0.19
10.0	10.02	+0.02
Tolerance Limit (pH unit)		±0.20

### Salinity

Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	--
10	9.57	-4.3
20	19.70	-1.5
30	29.86	-0.5
Tolerance Limit (%)		±10.0

### Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
11.0	11.4	+0.4
21.5	21.9	+0.4
38.0	38.3	+0.3
Tolerance Limit (°C)		±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

  
Mr. Fung Lim Chee, Richard  
General Manager  
Greater China & Hong Kong





ALS Technichem (HK) Pty Ltd  
11/F, Chung Shun Knitting Centre  
1-3 Wing Yip Street  
Kwai Chung, N.T., Hong Kong  
T: +852 2610 1044  
F: +852 2610 2021  
www.alsglobal.com

## REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

**CONTACT:** MR ALAN LI  
**CLIENT:** LAM ENVIRONMENTAL SERVICES LTD  
**ADDRESS:** 11/F., CENTRE POINT,  
181-185 GLOUCESTER ROAD,  
WAN CHAI, HONG KONG

**WORK ORDER:** HK1435131  
**LABORATORY:** HONG KONG  
**DATE RECEIVED:** 29/10/2014  
**DATE OF ISSUE:** 05/11/2014

### COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.

The "Next Calibration Date" is recommended according to best practice principals as practised by the ALS Hong Kong laboratory or quoted from relevant international standards.

Scope of Test: Dissolved Oxygen, pH, Salinity and Temperature  
Equipment Type: Multifunctional Meter  
Brand Name: YSI  
Model No.: Professional Plus  
Serial No.: 14E100105  
Equipment No.: --  
Date of Calibration: 31 October, 2014

### NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Fung Lim Chee, Richard  
General Manager -  
Greater China & Hong Kong

# REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

**Work Order:** HK1435131  
**Date of Issue:** 05/11/2014  
**Client:** LAM ENVIRONMENTAL SERVICES LTD



**Equipment Type:** Multifunctional Meter  
**Brand Name:** YSI  
**Model No.:** Professional Plus  
**Serial No.:** 14E100105  
**Equipment No.:** --  
**Date of Calibration:** 31 October, 2014

**Date of next Calibration:** 31 January, 2015

## Parameters:

### Dissolved Oxygen

**Method Ref:** APHA (21st edition), 4500O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
2.46	2.58	+0.12
5.04	4.91	-0.13
8.02	7.92	-0.10
Tolerance Limit (mg/L)		±0.20

### pH Value

**Method Ref:** APHA (21st edition), 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	3.98	-0.02
7.0	6.98	-0.02
10.0	10.05	+0.05
Tolerance Limit (pH unit)		±0.20

### Salinity

**Method Ref:** APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.00	--
10	9.58	-4.2
20	19.48	-2.6
30	30.32	+1.1
Tolerance Limit (%)		±10.0

### Temperature

**Method Ref:** Section 6 of International Accreditation New Zealand Technical  
**Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.**

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
13.4	13.7	+0.3
23.8	24.0	+0.2
33.8	33.6	-0.2
Tolerance Limit (°C)		±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

  
 Mr. Fung Lim Chee, Richard  
 General Manager  
 Greater China & Hong Kong



## EQUIPMENT PERFORMANCE CHECK / CALIBRATION REPORT

**Report No.** : HK1410306  
**Project Name** : EQUIPMENT PERFORMANCE CHECK/CALIBRATION REPORT  
**Date of Issue** : 16/10/2014  
  
**Customer** : LAM GEOTECHNICS LIMITED  
**Address** : 11/F., CENTRE POINT, 181-185 GLOUCESTER ROAD, WAN CHAI, HONG KONG


---

**Calibration Job No.** : HK1410306  
**Test Item No.** : HK1410306-01  
**Test Item Details**  
**Test Item Description** : Multifunctional Meter  
**Manufacturer** : YSI  
**Model No.** : YSI 600XL  
**Serial No.** : 05C1607  
**Test Item Receipt Date** : 13-Oct-14  
**Test Period** : 14/10/2014 - 15/10/2014

---

- Notes :
1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
  2. Results relate to item(s) as received.
  3.  $\pm$  indicates the tolerance limit
  4. N/A = Not applicable
  5. APHA - American Public Health Association, American Water Works Association and Water Environment Federation, Standard Methods for the Examination of Water and Wastewater, APHA-AWWA-WEF. USA
  6. DO, salinity, pH and temperature performance check was subcontracted to FT Laboratories Ltd.

Approved Signatory :

  
 \_\_\_\_\_  
 Peter Lee  
 (Director)

Issue Date:

16/10/2014





# REPORT OF EQUIPMENT PERFORMANCE CHECK

**WORK ORDER:** HK1410306  
**DATE OF ISSUE:** 16/10/2014  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type</b>	Multifunctional Meter
<b>Manufacturer</b>	YSI
<b>Model No.</b>	YSI 600XL
<b>Serial No.</b>	05C1607
<b>Date of Calibration</b>	14-Oct-14
<b>Date of next Calibration</b>	14-Jan-15

## Parameters:

### Temperature (Method Ref: APHA 19e 2550B)

Reference Reading (°C)	Temperature corrected of Thermometer (°C)	Display Reading (°C)	Deviation (°C)
10.21	10.37	10.33	-0.04
19.97	20.13	20.12	-0.01
30.02	30.18	30.16	-0.02
Tolerance Limit			±0.50

### pH Value (Method Ref: APHA 19e 4500-H, B)

Expected Reading (pH unit)	pH unit of buffer at 20 °C (pH unit)	Display Reading at 20 °C (pH unit)	Deviation (pH unit)
6.0	6.01	5.89	-0.12
9.0	9.02	8.85	-0.17
Tolerance Limit			±0.20

### Conductivity (Method Ref: APHA 19e 2520B)

KCl concentration (mol/L)	Standard conductivity (ms/cm) at 25°C	Reading of SpCond (ms/cm)	Deviation (%)
0.0000	0.00	0.00	--
0.1000	12.89	12.82	-0.54
0.2000	24.8	24.78	-0.08
0.5000	58.67	58.43	-0.41
Tolerance Limit			±2.0

### Dissolved Oxygen (DO) (Method Ref: (APHA 19e 4500-O, C)

DO of water sample (mg/L)	DO reading of DO probe (mg/L)	Deviation (mg/L)
4.15	3.98	-0.17
6.24	6.14	-0.10
8.16	8.15	-0.01
Tolerance Limit		±0.20

- Remarks:
- (1) Maximum tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.
  - (2) Displayed reading presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.
  - (3) Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

- End of Report -

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Jul 14, 2014 Rootsmeter S/N 0438320 Ta (K) - 298  
Operator Tisch Orifice I.D. - 0005 Pa (mm) - 749.3

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.3870	3.2	2.00
2	NA	NA	1.00	0.9830	6.4	4.00
3	NA	NA	1.00	0.8760	7.9	5.00
4	NA	NA	1.00	0.8340	8.8	5.50
5	NA	NA	1.00	0.6860	12.7	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9817	0.7078	1.4042	0.9957	0.7179	0.8919
0.9775	0.9944	1.9859	0.9915	1.0086	1.2613
0.9754	1.1135	2.2203	0.9894	1.1294	1.4101
0.9743	1.1683	2.3286	0.9882	1.1849	1.4790
0.9692	1.4128	2.8084	0.9830	1.4330	1.7837
Qstd slope (m) = 1.99175			Qa slope (m) = 1.24720		
intercept (b) = -0.00041			intercept (b) = -0.00026		
coefficient (r) = 0.99991			coefficient (r) = 0.99991		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)  
Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]  
Qa = Va/Time

For subsequent flow rate calculations:

Qstd = 1/m{ [SQRT(H2O(Pa/760) (298/Ta))] - b}  
Qa = 1/m{ [SQRT H2O(Ta/Pa)] - b}



Lam Geotechnics Limited

**Calibration Data for High Volume Sampler (TSP Sampler)**

Location : CMA3a

Equipment no. : EL333

Calibration Date : 21-Oct-14

Calibration Due Date : 21-Dec-14

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	303	Kelvin	Pressure, P <sub>a</sub>
			1015 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041
Last Calibration Date	14-Jul-14	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	14-Jul-15				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.)  X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31)  Y-axis
	(up)	(down)	(difference)			
1	5.4	5.4	10.8	1.6379	54	53.5975
2	4.1	4.1	8.2	1.4272	49	48.6348
3	3.1	3.1	6.2	1.2410	42	41.6869
4	2.0	2.0	4.0	0.9969	37	36.7242
5	1.2	1.2	2.4	0.7722	31	30.7689

By Linear Regression of Y on X

Slope, m = 26.5451      Intercept, b = 10.0291

Correlation Coefficient\* = 0.9965

Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient &lt; 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

\_\_\_\_\_

Calibrated by : Henry Lau

Date : 21-Oct-14

Checked by : Derek Lo

Date : 21-Oct-14



Lam Geotechnics Limited

**Calibration Data for High Volume Sampler (TSP Sampler)**

Location : CMA3a

Equipment no. : EL333

Calibration Date : 18-Dec-14

Calibration Due Date : 18-Feb-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	287	Kelvin	Pressure, P <sub>a</sub>
			1026 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041
Last Calibration Date	14-Jul-14	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	14-Jul-15				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	5.5	5.5	11.0	1.7076	56	57.4196
2	4.3	4.3	8.6	1.5099	47	48.1914
3	3.2	3.2	6.4	1.3026	44	45.1154
4	2.5	2.5	5.0	1.1513	38	38.9633
5	1.2	1.2	2.4	0.7977	25	25.6337

By Linear Regression of Y on X

Slope, m = 33.6450      Intercept, b = -0.4658

Correlation Coefficient\* = 0.9920

Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient &lt; 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

\_\_\_\_\_

Calibrated by : Henry Lau

Date : 18-Dec-14

Checked by : Derek Lo

Date : 18-Dec-14



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

## ***Appendix 5.1***

### ***Monitoring Schedules for Reporting Month and Coming Reporting Month***



**Wan Chai Development Phase II and Central-Wan Chai Bypass  
Sampling, Field Measurement and Testing Works (Stage 2)**

**Environmental Monitoring Schedule  
December 2014**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					28-Nov	29-Nov
30-Nov	1-Dec	2-Dec	3-Dec	4-Dec	5-Dec	6-Dec
		24hr TSP Noise (Daytime)	1hr TSP			
7-Dec	8-Dec	9-Dec	10-Dec	11-Dec	12-Dec	13-Dec
	Noise (Daytime)	24hr TSP 1hr TSP				
14-Dec	15-Dec	16-Dec	17-Dec	18-Dec	19-Dec	20-Dec
	24hr TSP 1hr TSP	Noise (Daytime)			24hr TSP	1hr TSP
21-Dec	22-Dec	23-Dec	24-Dec	25-Dec	26-Dec	27-Dec
	Noise (Daytime)	24hr TSP	1hr TSP			
	Impact WQM Mid-ebb 0:00 Mid-flood 7:06		Impact WQM Mid-ebb 1:28 Mid-flood 8:34		Impact WQM Mid-ebb 2:59 Mid-flood 10:08	

Remark: As informed by CWB RSS, the operation of diverted Windsor House cooling intake was commenced on 20 Dec 2014 and the water quality monitoring at monitoring station C7 for Windsor House Colling water intake was resumed on 22 Dec 2014

**Wan Chai Development Phase II and Central-Wan Chai Bypass  
Sampling, Field Measurement and Testing Works (Stage 2)**

**Tentive Environmental Monitoring Schedule  
January 2015**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
28-Dec	29-Dec	30-Dec	31-Dec	1-Jan	2-Jan	3-Jan
	24hr TSP Noise (Daytime)	1hr TSP Noise (Daytime)				24hr TSP
	Impact WQM		Impact WQM			Impact WQM
	Mid-ebb 5:41		Mid-flood 14:24			Mid-flood 16:41
	Mid-flood 12:40		Mid-ebb 21:29			Mid-ebb 23:43
4-Jan	5-Jan	6-Jan	7-Jan	8-Jan	9-Jan	10-Jan
	1hr TSP Noise (Daytime)	Noise (Daytime)			24hr TSP	1hr TSP
		Impact WQM		Impact WQM		Impact WQM
		Mid-ebb 0:55		Mid-ebb 1:59		Mid-ebb 2:50
		Mid-flood 7:53		Mid-flood 8:53		Mid-flood 9:56
11-Jan	12-Jan	13-Jan	14-Jan	15-Jan	16-Jan	17-Jan
	Noise (Daytime)	Noise (Daytime)		24hr TSP	1hr TSP	
	Impact WQM		Impact WQM		Impact WQM	
	Mid-ebb 3:36		Mid-flood 12:39		Mid-flood 14:16	
	Mid-flood 11:15		Mid-ebb 19:32		Mid-ebb 21:46	
18-Jan	19-Jan	20-Jan	21-Jan	22-Jan	23-Jan	24-Jan
	Noise (Daytime)	Noise (Daytime)	24hr TSP	1hr TSP		
	Impact WQM		Impact WQM		Impact WQM	
	Mid-flood 16:49		Mid-ebb 13:07		Mid-flood 8:52	
	Mid-ebb 23:47		Mid-flood 18:33		Mid-ebb 14:38	
25-Jan	26-Jan	27-Jan				
	Noise (Daytime)	24hr TSP Noise (Daytime)				
	Impact WQM					
	Mid-flood 11:05					
	Mid-ebb 17:20					



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

## ***Appendix 5.2***

### ***Noise Monitoring Results and Graphical Presentations***



**Noise Monitoring Result**

**Day Time (0700 - 1900hrs on normal weekdays)**

Location: M2b - Noon-day gun area

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30-min)								
02/12/14	16:50	Cloudy	69.0	70.5	67.2	68	63	75
08/12/14	14:48	Fine	69.4	70.5	67.0	68	65	75
16/12/14	11:18	Fine	70.0	74.2	66.5	68	66	75
22/12/14	10:20	Fine	68.4	69.5	66.0	68	61	75




Contract No. HK/2011/07

Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter)

### Graphic Presentation of Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

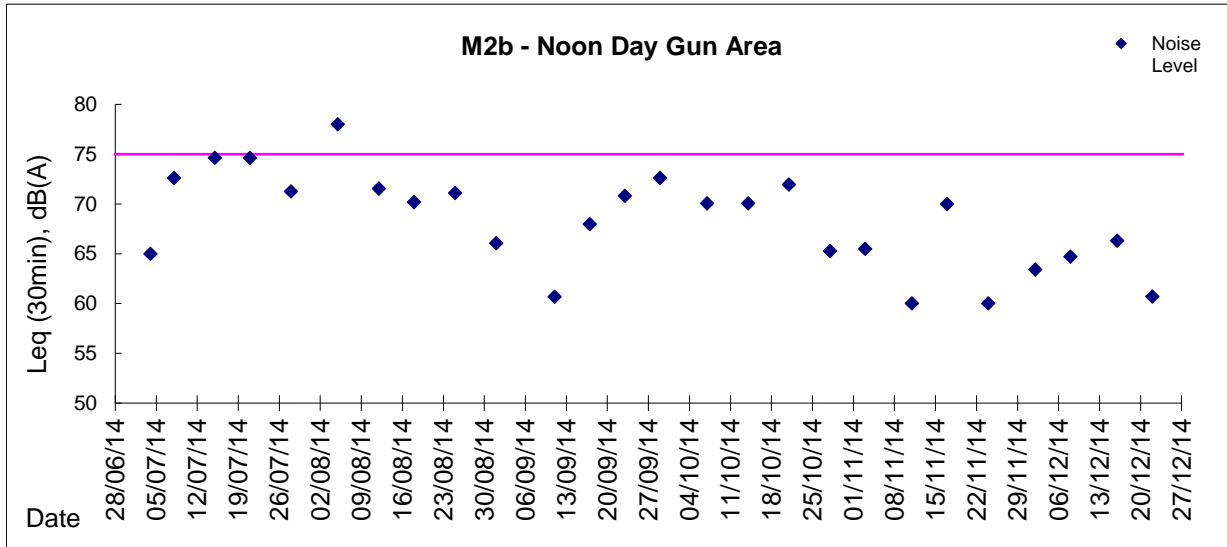



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

### ***Appendix 5.3***

#### ***Air Quality Monitoring Results and Graphical Presentations***

Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring

Action Level ( $\mu\text{g}/\text{m}^3$ ) - 171

Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{\text{si}}$	Final, $Q_{\text{sf}}$	Average		
2-Dec-14	8:00	Cloudy	010207	2.7508	2.8062	2644.55	2668.55	24.00	1.19	1.18	1.19	1709	32
9-Dec-14	15:47	Fine	009885	2.7675	3.0046	2674.55	2698.55	24.00	1.19	1.23	1.21	1742	136
15-Dec-14	15:00	Fine	010725	2.7132	3.0062	2701.55	2725.55	24.00	1.29	1.29	1.29	1857	158
19-Dec-14	8:00	Rainy	010726	2.7169	2.8030	2725.55	2749.55	24.00	1.26	1.26	1.26	1813	47
23-Dec-14	8:00	Cloudy	010782	2.7131	2.8959	2752.55	2776.55	24.00	1.14	1.13	1.14	1638	112

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 8 and 13 December 2014 to 9 and 15 December 2014 respectively.

Report on 1-hour TSP monitoring

Action Level ( $\mu\text{g}/\text{m}^3$ ) - 311.3

Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 500


Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{\text{si}}$	Final, $Q_{\text{sf}}$	Average		
3-Dec-14	8:24	Cloudy	010598	2.7248	2.7339	2668.55	2669.55	1.00	1.16	1.16	1.16	70	131
3-Dec-14	9:30	Cloudy	010599	2.7278	2.7351	2669.55	2670.55	1.00	1.01	1.01	1.01	61	120
3-Dec-14	10:55	Cloudy	010527	2.7111	2.7180	2670.55	2671.55	1.00	1.16	1.16	1.16	70	99
9-Dec-14	10:30	Fine	010600	2.7268	2.7361	2671.55	2672.55	1.00	1.09	1.09	1.09	65	142
9-Dec-14	13:00	Fine	010192	2.7614	2.7706	2672.55	2673.55	1.00	1.02	1.02	1.02	61	151
9-Dec-14	14:25	Fine	010202	2.7701	2.7782	2673.55	2674.55	1.00	1.02	1.09	1.05	63	128
15-Dec-14	9:50	Fine	010720	2.7274	2.7374	2698.55	2699.55	1.00	1.16	1.16	1.16	70	143
15-Dec-14	10:52	Fine	010722	2.7201	2.7282	2699.55	2700.55	1.00	1.09	1.09	1.09	65	124
15-Dec-14	13:00	Fine	010723	2.7292	2.7375	2700.55	2701.55	1.00	1.16	1.16	1.16	70	119
20-Dec-14	8:36	Rainy	010777	2.7074	2.7122	2749.55	2750.55	1.00	1.27	1.27	1.27	76	63
20-Dec-14	9:43	Rainy	010779	2.7231	2.7296	2750.55	2751.55	1.00	1.27	1.27	1.27	76	86
20-Dec-14	10:51	Rainy	010781	2.7269	2.7295	2751.55	2752.55	1.00	1.12	1.12	1.12	67	39
24-Dec-14	8:30	Cloudy	010809	2.7382	2.7430	2776.55	2777.55	1.00	1.11	1.11	1.11	67	72
24-Dec-14	9:35	Cloudy	010810	2.7415	2.7478	2777.55	2778.55	1.00	1.11	1.11	1.11	67	94
24-Dec-14	10:50	Cloudy	010813	2.7233	2.7328	2778.55	2779.55	1.00	1.11	1.11	1.11	67	142




Contract No. HK/2011/07

Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter)

### Graphic Presentation of 1 hour TSP Result

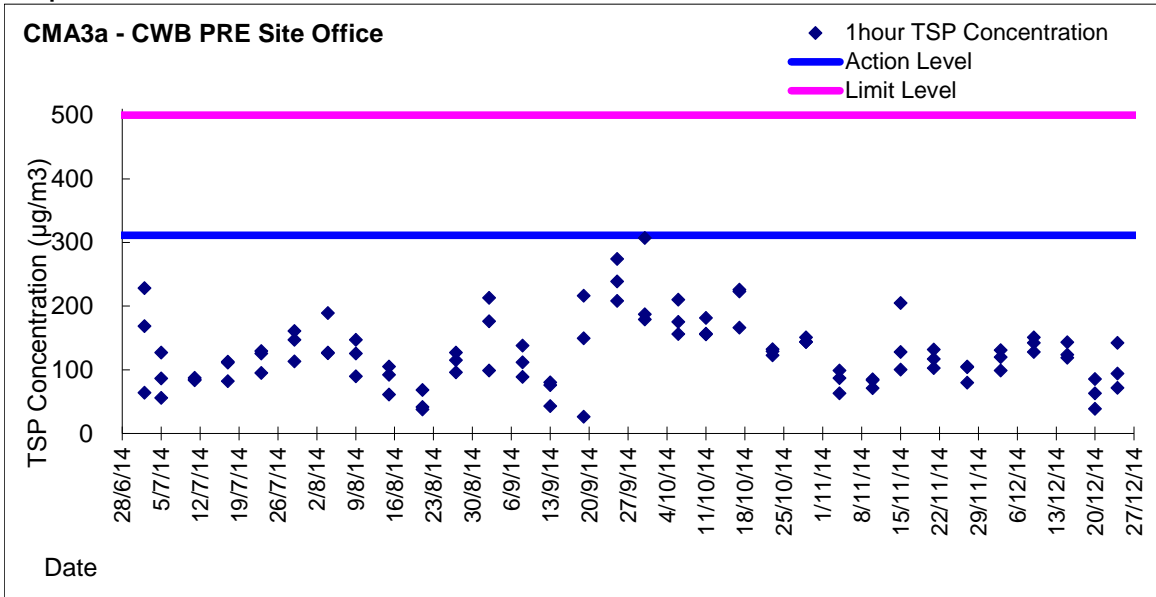

### Graphic Presentation of 24 hour TSP Result

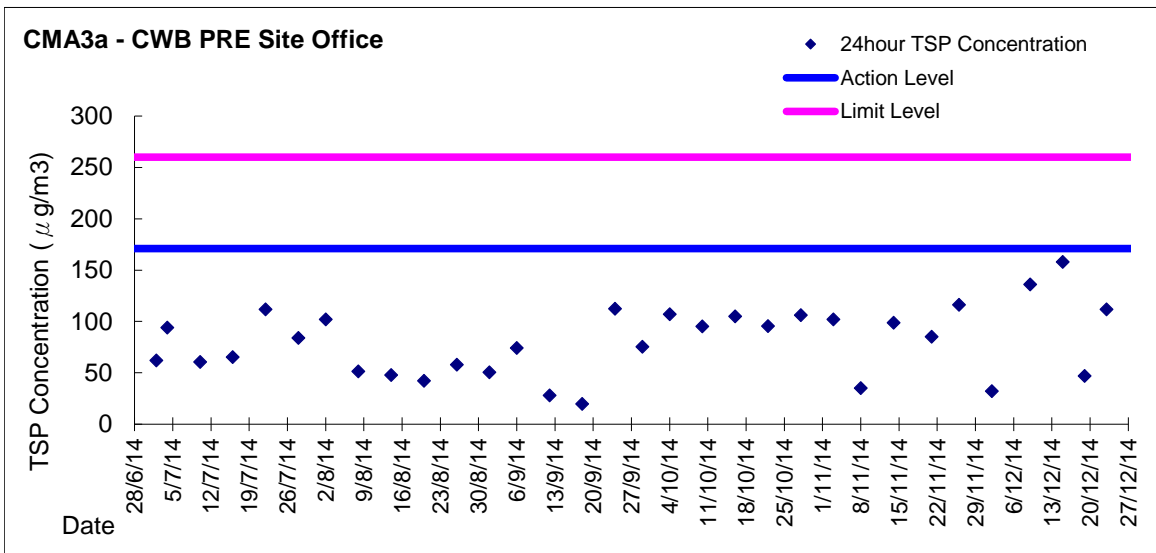





**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

***Appendix 5.4***  
***Water Quality Monitoring Results and Graphical Presentation***

---



**Water Monitoring Result at C7 - Windsor House**  
**Mid-Flood Tide**

Date	Time	Weater Condition	Sampling Depth		Water Temperature		pH		Salinity		DO Saturation		DO		Turbidity		Suspended Solids							
			m		°C		-		ppt		%		mg/L		NTU		mg/L							
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average						
22/12/14	7:58	Fine	-	-	17.10	17.10	17.00	8.28	8.28	8.28	31.75	31.75	31.75	83.7	86.7	86.0	6.68	6.91	6.86	4.89	4.82	4.84	<2	<2
	8:00		-	-	16.90	16.90		8.27	8.27		31.76	31.75		86.7	87.0		6.91	6.95		4.84	4.80		<2	
24/12/14	7:32	Fine	-	-	18.00	18.00	18.00	8.24	8.24	8.24	31.49	31.49	31.50	88.1	88.0	87.9	6.91	6.90	6.89	2.84	2.85	2.85	5	4.50
	7:34		-	-	18.00	18.00		8.24	8.24		31.50	31.50		88.3	87.0		6.93	6.83		2.84	2.85		4	
26/12/14	10:35	Cloudy	-	-	17.80	17.80	17.80	8.11	8.11	8.11	31.69	31.69	31.69	84.5	84.9	84.8	6.76	6.80	6.79	1.98	2.08	2.10	3	3.00
	10:36		-	-	17.80	17.80		8.11	8.11		31.69	31.69		84.9	84.7		6.80	6.78		2.20	2.15		3	

Remarks:  
 Single underline denotes exceedance over Action Level.  
 Double underline denotes exceedance over Limit Level.






**Water Monitoring Result at C7 - Windsor House**  
**Mid-Ebb Tide**

Date	Time	Weater Condition	Sampling Depth		Water Temperature °C		pH -		Salinity ppt		DO Saturation %		DO mg/L		Turbidity NTU		Suspended Solids mg/L	
			m		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average
22/12/14	23:18	Cloudy	-	-	15.30	15.30	8.02	8.02	31.45	31.48	88.0	88.1	7.27	7.29	1.79	1.71	2	2.00
	23:19		-	-	15.30	15.30	8.03	8.03	31.49	31.49	88.3	88.4	7.30	7.32	1.67	1.64	2	2.00
24/12/14	0:12	Cloudy	-	-	17.40	17.40	7.77	7.77	31.58	31.58	92.8	92.5	7.35	7.33	1.61	1.52	<2	<2
	0:13		-	-	17.40	17.40	7.79	7.79	31.57	31.57	92.2	91.8	7.30	7.27	1.50	1.56	<2	<2
26/12/14	2:50	Cloudy	-	-	17.30	17.30	8.06	8.06	31.69	31.69	93.2	93.0	7.39	7.38	3.25	3.27	2	2.00
	2:51		-	-	17.30	17.30	8.07	8.07	31.67	31.67	91.6	92.0	7.25	7.29	3.23	3.11	2	2.00

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



## Graphic Presentation of Water Quality Result of C7 - Windsor House

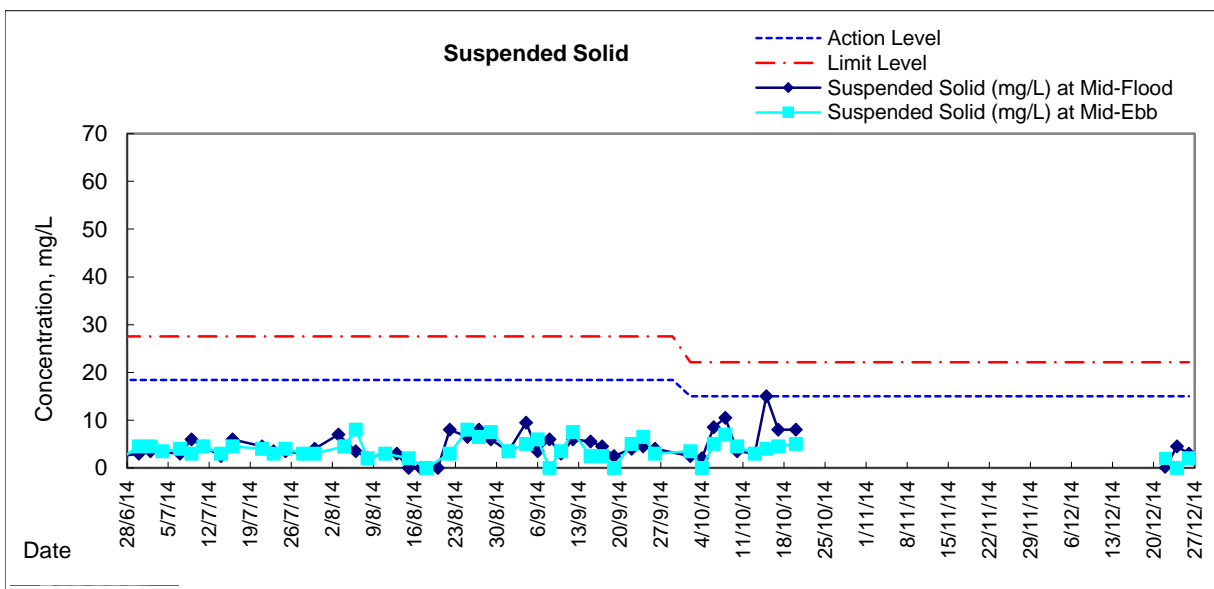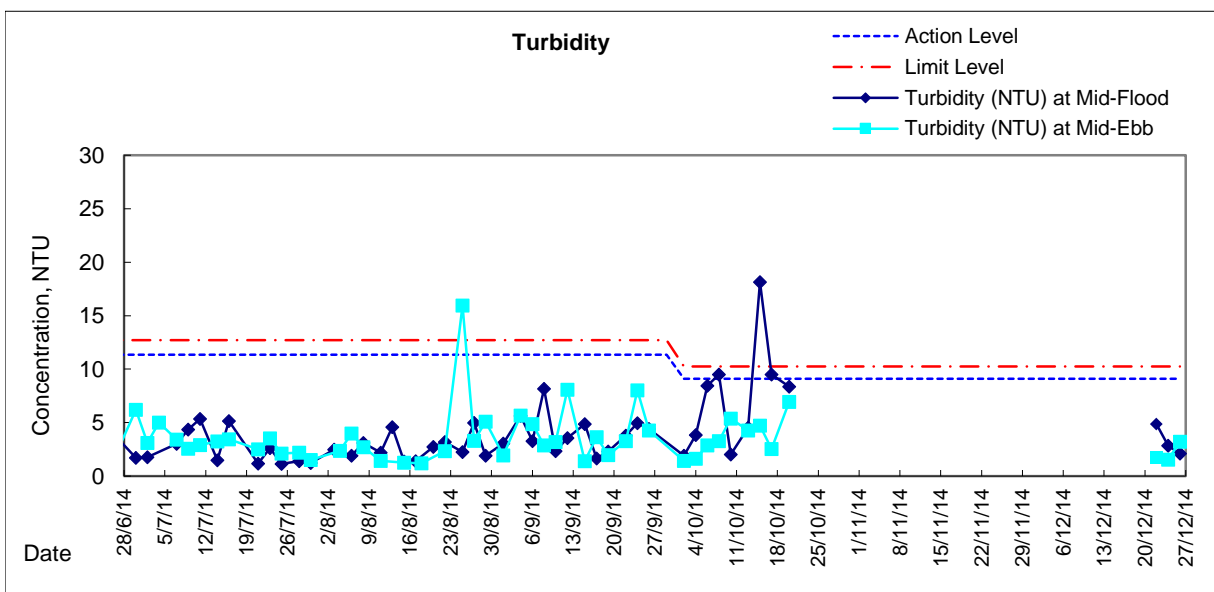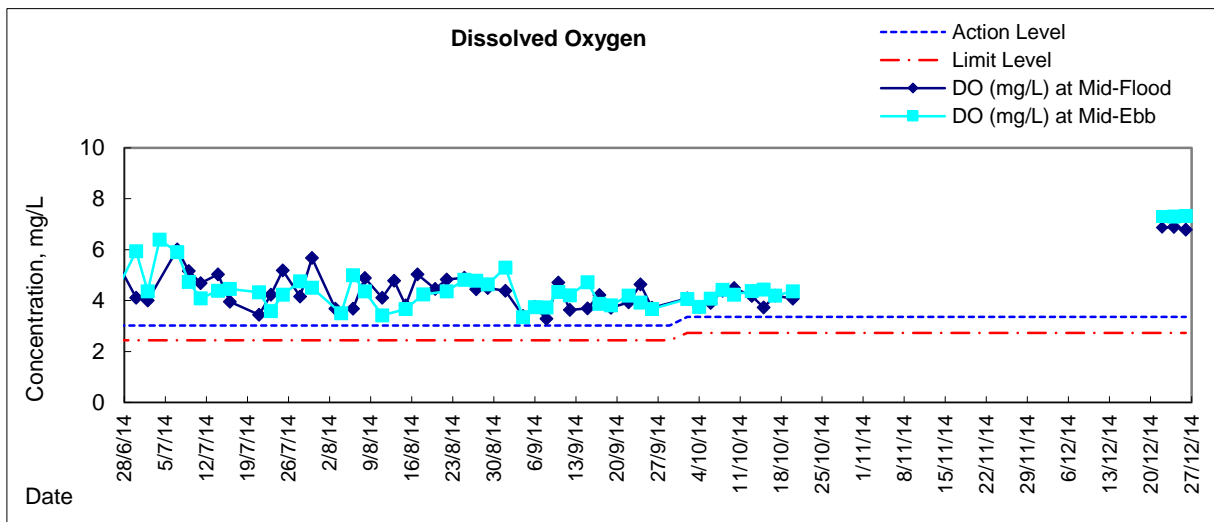



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

## ***Appendix 6.1***

### ***Event Action Plans***



Lam Geotechnics Limited

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
<b>Action Level</b>	1. Notify IEC, ER and Contactor 2. Carry out investigation 3. Report the results of investigation to the IEC, ER and Contactor 4. Discuss with the IEC and Contractor on remedial measures required 5. Increase monitoring frequency to check mitigation effectiveness (The above actions should be taken within 2 working days after the exceedance is identified)	1. Review the investigation results submitted by the ET 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly 3. Advise the ER on the effectiveness of the proposed remedial measures (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing 2. Notify Contractor 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented 4. Supervise the implementation of remedial measures (The above actions should be taken within 2 working days after the exceedance is identified)	1. Submit noise mitigation proposals to IEC and ER 2. Implement noise mitigation proposals (The above actions should be taken within 2 working days after the exceedance is identified)
<b>Limit Level</b>	1. Inform IEC, ER, EPD and Contractor 2. Repeat measurement to confirm findings 3. Increase monitoring frequency 4. Identify source and investigate the cause of exceedance 5. Carry out analysis of Contractor's working procedures. Discuss with the IEC, Contractor and ER on remedial measures require 6. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results 7. If exceedance stops, cease additional monitoring (The above actions should be taken within 2 working days after the exceedance is identified)	1. Discuss amongst ER, ET and Contractor on the potential remedial actions 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing 2. Notify Contractor 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented 4. Supervise the implementation of remedial measures 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated (The above actions should be taken within 2 working days after the exceedance is identified)	1. Take immediate action to avoid further exceedance 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification 3. Implement the agreed proposals 4. Submit further proposal if problem still not under control 5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated (The above actions should be taken within 2 working days after the exceedance is identified)



Lam Geotechnics Limited

Contract No. HK/2011/07

Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

Event / Action Plan for Construction Air Quality

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
<b>ACTION LEVEL</b>				
1. Exceedance for one sample	1. Identify source, investigate the causes of complaint and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Notify Contractor. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified.)
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Submit proposals for remedial to ER within three working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified.)
<b>LIMIT LEVEL</b>				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC, ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified.)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within three working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified.)



Lam Geotechnics Limited

Contract No. HK/2011/07

Wanchai Development Phase II and Central Wanchai Bypass

(Shatin to Central Link (SCL) Protection

Works at Causeway Bay Typhoon Shelter)

2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"><li>1. Notify IEC, ER, Contractor and EPD;</li><li>2. Identify source;</li><li>3. Repeat measurement to confirm findings;</li><li>4. Increase monitoring frequency to daily;</li><li>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li><li>6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li><li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li><li>8. If exceedance stops, cease additional monitoring.</li></ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"><li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li><li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li><li>3. Supervise the implementation of remedial measures.</li></ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"><li>1. Confirm receipt of notification of failure in writing;</li><li>2. Notify Contractor;</li><li>3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li><li>4. Ensure remedial measures properly implemented;</li><li>5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li></ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>	<ol style="list-style-type: none"><li>1. Take immediate action to avoid further exceedance;</li><li>2. Submit proposals for remedial actions to IEC within three working days of notification;</li><li>3. Implement the agreed proposals;</li><li>4. Resubmit proposals if problem still not under control;</li><li>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li></ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified.)</p>
---	--	---	---	--





Event and Action Plan for Marine Water Quality

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Action level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next working day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Limit level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures; As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities. (The above actions should be taken within 1 working day after the exceedance is identified)



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

## ***Appendix 6.2***

### *Summary of Notification of Exceedances*



Contract No. HK/2011/07

Wanchai Development Phase II and Central Wanchai Bypass  
Sampling, Field Measurement and Testing Work (Stage 2)

### Summary for Notification of Exceedance

[illegible]



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

## ***Appendix 7.1***

### ***Complaint Log***



Lam Geotechnics Limited

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection Works at Causeway Bay Typhoon Shelter)

### ***Environmental Complaints Log***

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
--	--	--	--	--	--	--



**Lam Geotechnics Limited**

Contract No. HK/2011/07  
Wanchai Development Phase II and Central Wanchai Bypass  
(Shatin to Central Link (SCL) Protection  
Works at Causeway Bay Typhoon Shelter)

---

## ***Appendix 8.1***

### ***Construction Programme of Individual Contracts***

WP13-0

Activity ID

Activity Name

Calendar

Original Duration

Start

Finish

Total Float

Q4

Q1

Q2

Q3

Q4

Q1

Q2

Q3

Q4

Q1

Q2

Q3

Q4

Date Printed 26-Sep-14 11

HY/2009/15 - Works Programme Rev. M (DD:20-Sep-12)

Works in East Ventilation Adit - Based on Alternative Method

Reinstatement of Breakwater

S3\_54840

Reinstatement works -west side

7d/wk-1

60d

21-Feb-14 08 A

30-Sep-14 18

-85d

1 of 18

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Prepared by William Caluza			
Date	Revision	Checked	Approved
26-Sep-14	1st submission		

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

中國建築工程(香港)有限公司  
CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016							
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
Stage 7 (Zones C & E - ME4-D06 to D01, SCL1 & TS4-D25)																		
A-4000	Marine removal of temporary reclamation and seawall blocks (Zones C & E)	7d/wk-2	18d	06-Sep-14 08 A	06-Oct-14 18	-353d												
A-3090	Hole coring (Qty: 44 nos)	7d/wk-2	9d	20-Sep-14 08*	28-Sep-14 18	-346d												
A-4010	D-Wall vertical cutting (Qty: 27pcs.)	7d/wk-2	7d	07-Oct-14 08	13-Oct-14 18	-353d												
A-4020	D-Wall horizontal cutting (Qty: 37 pcs.)	7d/wk-2	10d	11-Oct-14 08	20-Oct-14 18	-353d												
Stage 8 (Zone I - TS4-D01 to TS4-D08)																		
A-3050	Remaining removal of temporary reclamation (Zone I)	7d/wk-2	28d	29-Aug-14 08 A	01-Oct-14 18	-342d												
A-3060	Hole coring (Qty: 25 nos)	7d/wk-2	5d	02-Oct-14 08	06-Oct-14 18	-342d												
A-3070	D-Wall vertical cutting (Qty: 14 pcs.)	7d/wk-2	3d	07-Oct-14 08	09-Oct-14 18	-342d												
A-3080	D-Wall horizontal cutting (Qty: 24 pcs.)	7d/wk-2	5d	21-Oct-14 08	25-Oct-14 18	-353d												
Stage 9 (Zones G & K - TS4-D24 to TS4-D15)																		
A-4040	Relocation of RHKYC floating pontoon	7d/wk-2	5d	22-Sep-14 08*	26-Sep-14 18	-338d												
A-4050	Hole coring (Qty: 27 nos)	7d/wk-2	6d	29-Sep-14 08	04-Oct-14 18	-346d												
A-4060	Marine removal of temporary reclamation and seawall blocks (Zone G & K)	7d/wk-2	14d	11-Oct-14 08	24-Oct-14 18	-352d												
A-4070	D-Wall vertical cutting (Qty: 18pcs.)	7d/wk-2	4d	25-Oct-14 08	28-Oct-14 18	-352d												
A-4080	D-Wall horizontal cutting (Qty: 25 pcs.)	7d/wk-2	7d	26-Oct-14 08	01-Nov-14 18	-352d												
Stage 10 (Zone J - TS4-D09 to TS4-D14)																		
A-4090	Land removal of temporary reclamation (Zone J)	7d/wk-2	10d	07-Oct-14 08	16-Oct-14 18	-344d												
A-5000	Hole coring (Qty: 32 nos)	7d/wk-2	7d	17-Oct-14 08	23-Oct-14 18	-340d												
A-5010	Marine removal of temporary reclamation (Zone J)	7d/wk-2	7d	26-Oct-14 08	01-Nov-14 18	-353d												
A-5020	D-Wall vertical cutting (Qty: 20 pcs.)	7d/wk-2	5d	02-Nov-14 08	06-Nov-14 18	-353d												
A-5030	D-Wall horizontal cutting (Qty: 26 pcs.)	7d/wk-2	7d	04-Nov-14 08	10-Nov-14 18*	-353d												
Stage 13 - Phase 3 Mooring																		
A-5050	Final trimming of sea bed level	7d/wk-2	4d	02-Nov-14 08	05-Nov-14 18	-347d												
A-5060	Phase 3 Mooring	7d/wk-2	6d	06-Nov-14 08	11-Nov-14 18	-347d												
A-5040	Reinstatement of existing seawall (Zones I & J)	7d/wk-2	7d	11-Nov-14 08	17-Nov-14 18	-353d												
Stage 12 - Re-provisioning of Jetty																		
SS_5258	Provision of Mobile Crane (until permanent re-provision of Jetty is completed)	7d/wk-1	160d	20-Feb-14 08 A	30-Dec-14 18	-335d												
A-5010	BAS submission and consent for commencement of superstructure	7d/wk-2	28d	20-Sep-14 08 A	15-Oct-14 18	-336d												
Summary Bar							Prepared by William Caluza											
Actual Level of Effort							Date			Revision			Checked			Approved		
Actual Work							28-Sep...			1st submission								
Remaining Work																		
Critical Remaining Work																		
Milestone																		
China State Construction Engineering (Hong Kong) Ltd														中國建築工程(香港)有限公司				
Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel / Causeway Bay Typhoon Shelter Section)														CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.				
WORKS PROGRAMME REV. M																		

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A-6012	Submission of performance report	7d/wk-2	1d	25-Oct-14 08*	25-Oct-14 18	-286d	I Submission of performance report  ■ Erection of working platform for jetty beams and reinstate the floating pontoon I BA10 submission for authorized signatory and subcontractor ■ Jetty beams construction ■ Construction of floating pontoon ■ BA13 submission + 14-day cube test results ■ EAM and accessories installation Handover to RHKYC							
A-6020	Erection of working platform for jetty beams and reinstate the floating pontoon	7d/wk-2	10d	02-Nov-14 08	11-Nov-14 18	-352d								
A-6040	BA10 submission for authorized signatory and subcontractor	7d/wk-2	1d	12-Nov-14 08	12-Nov-14 18	-304d								
A-6030	Jetty beams construction	7d/wk-2	14d	12-Nov-14 08	25-Nov-14 18	-352d								
A-6052	Construction of floating pontoon	7d/wk-2	14d	26-Nov-14 08	09-Dec-14 18	-331d								
A-6050	BA13 submission + 14-day cube test results	7d/wk-2	28d	26-Nov-14 08	23-Dec-14 18	-352d								
A-6060	EAM and accessories installation	7d/wk-2	7d	24-Dec-14 08	30-Dec-14 18	-352d								
A-6070	Handover to RHKYC	7d/wk-2	1d	31-Dec-14 08	31-Dec-14 18	-352d								
Stage 11 - Construction of TZ4														
A-6080	South side - laying rockfill and levelling stone (Qty: 1,550 cu.m)	7d/wk-2	12d	24-Sep-14 08	05-Oct-14 18	-339d		■ South side - laying rockfill and levelling stone (Qty: 1,550 cu.m)						
A-6090	South side - install seawall blocks (Qty: 255 nos.)	7d/wk-2	6d	05-Oct-14 08	11-Oct-14 18	-339d	■ South side - install seawall blocks (Qty: 255 nos.)							
A-7000	South side - general fill (Qty: 2,000 cu.m.)	7d/wk-2	2d	12-Oct-14 08	13-Oct-14 18	-339d	■ South side - general fill (Qty: 2,000 cu.m.)							
A-7010	North side - laying rockfill and levelling stone (Qty: 1,550 cu.m)	7d/wk-2	12d	21-Oct-14 08	01-Nov-14 18	-346d	■ North side - laying rockfill and levelling stone (Qty: 1,550 cu.m)							
A-7020	North side - install seawall blocks (Qty: 255 nos.)	7d/wk-2	6d	02-Nov-14 08	07-Nov-14 18	-346d	■ North side - install seawall blocks (Qty: 255 nos.)							
A-7030	North side - general fill (Qty:2,000 cu.m.)	7d/wk-2	2d	08-Nov-14 08	09-Nov-14 18	-346d	■ North side - general fill (Qty:2,000 cu.m.)							
A-7040	Handover to contract TS3/SR8	7d/wk-2	1d	10-Nov-14 08	10-Nov-14 18*	-346d	■ Handover to contract TS3/SR8							
TS4/ME4, Removal of Temporary Reclamation														
SZ6875	Completion of Section 2 (With ME4 option) (KD7)	7d/wk-2	0d		17-Nov-14 18	-353d	◆ Completion of Section 2 (With ME4 option) (KD7)							
SZ6890	Completion of Section 7B (ME4) (KD13)	7d/wk-2	0d		17-Nov-14 18	-353d	◆ Completion of Section 7B (ME4) (KD13)							
TS4 - OHVD / Cable Trough														
S5_6185	TS4 (incl. TS4+) - OHVD Slab - Area C (access through temp. opening at TZ4)	7d/wk-1	36d	02-Jan-15 08*	05-Feb-15 18	195d	■ TS4 (incl. TS4+) - OHVD Slab - Area C (access through temp. opening at TZ4)							
S5_6190	TS4 (incl. TS4+) - Cable Trough (access through temp. opening at TZ4)	7d/wk-1	60d	07-Feb-15 08*	14-Apr-15 18	195d	■ TS4 (incl. TS4+) - Cable Trough (access through temp. opening at TZ4)							
S5_59850	Completion of Section 5 - TS4/ME4 Area (KD10), below -20mPD	7d/wk-2	0d		02-Nov-15 18*	0d	◆ Completion of Section 5 - TS4/ME4 Area (KD10), below -20mPD							
Works in TPCWAE Area (Portion 20A, 20B)														
Removal of Temporary Reclamation														
Removal of Temporary Reclamation & Form TZ5														
S67670	Remove general fill / sea wall block	7d/wk-1	24d	20-May-14 08 A	08-Oct-14 18	-296d	■ Remove general fill / sea wall block							
S67675	Diaphragm wall saw cutting (1st D Wall cut on 23 Jun 2014)	7d/wk-1	31d	03-Sep-14 08 A	16-Oct-14 18	-306d	■ Diaphragm wall saw cutting (1st D Wall cut on 23 Jun 2014)							
S67755	Form TZ5	7d/wk-1	18d	25-Sep-14 08	14-Oct-14 18	-304d	■ Form TZ5							
Summary Bar														
Actual Level of Effort														
Actual Work														
Remaining Work														
Critical Remaining Work														
Milestone														
Prepared by William Caluza														
Date														
26-Sep... 1st submission														
Revision														
Checked														
Approved														
China State Construction Engineering (Hong Kong) Ltd														
Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)														
WORKS PROGRAMME REV. M														
3 of 18														
中國建築工程(香港)有限公司														
CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.														



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016				
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
S67685	Achievement of KD5	7d/wk-2	0d		16-Oct-14 18	-323d	◆ Achievement of KD5								
S67687	Complete Reinstatement of Vertical Seawall (near PRE Office)	7d/wk-2	0d		27-Oct-14 18	-322d	◆ Complete Reinstatement of Vertical Seawall (near PRE Office)								
Reinstate Mucking Out Access Shaft "C"															
S67240	Start reinstatement works (after completion of TPCWAW OHVD works)	6d/wk	0d	28-Mar-16 08		-102d								◆ Start reinstatement works (after c	
S67225	Cast slab opening at top of CCT West bound (access shaft)	6d/wk	18d	28-Mar-16 08	16-Apr-16 18	-102d								Cast slab opening at top of C	
S67230	Removal of vertical shaft and backfilling	6d/wk	48d	11-Apr-16 08	04-Jun-16 18	-102d								Removal of vertical	
S67235	Reinstatement of pavement	6d/wk	12d	30-May-16 08	11-Jun-16 18	-102d								Reinstatement of	
TPCWAE - OHVD / Cable Trough															
S5_7405	TPCWAE - Cable Trough (access through temp. opening at TZS & Portion 19)	6d/wk	48d	04-Sep-15 08	02-Nov-15 18	0d								TPCWAE - Cable Trough (access through temp. opening at T	
S5_7400	TPCWAE - OHVD Slab AT Area A (access through temp. opening at TZS & Portion 19)	6d/wk	48d	04-Sep-15 08	02-Nov-15 18	0d								TPCWAE - OHVD Slab AT Area A (access through temp. open	
S5_59840	Completion of Section 5 - TPCWAE Area (KD10), below -20mPD	7d/wk-2	0d		02-Nov-15 18*	0d								◆ Completion of Section 5 - TPCWAE Area (KD10), below -20m	
Works in TPCWAW Area															
TPCWAW - Temporary Reclamation															
Temporary Reclamation -															
S6_9440	TPCWAW - place levelling stone and tamping, South side	7d/wk-1	6d	15-Oct-14 08	20-Oct-14 18	-122d	■ TPCWAW - place levelling stone and tamping, South side								
S6_9450	TPCWAW - place seawall block to +4 at South side (Qty: 569 nos. @ 50 nos/day)	7d/wk-1	12d	21-Oct-14 08	01-Nov-14 18	-122d	■ TPCWAW - place seawall block to +4 at South side (Qty: 569 nos. @ 50 nos/day)								
S6_9465	TPCWAW - place levelling stone and tamping, North side	7d/wk-1	6d	02-Nov-14 08	07-Nov-14 18	-122d	■ TPCWAW - place levelling stone and tamping, North side								
S6_9470	TPCWAW - place seawall blocks to +4 North side (Qty:572 nos @ 50 nos/day)	7d/wk-1	14d	08-Nov-14 08	21-Nov-14 18	-122d	■ TPCWAW - place seawall blocks to +4 North side (Qty:572 nos @ 50 nos/day)								
S6_9495	TPCWAW - General fill to +2 within the seawall	7d/wk-1	17d	15-Nov-14 08	01-Dec-14 18	-122d	■ TPCWAW - General fill to +2 within the seawall								
S6_9490	TPCWAW - place seawall blocks to +4 at the temporary opening	7d/wk-1	7d	02-Dec-14 08	08-Dec-14 18	-122d	■ TPCWAW - place seawall blocks to +4 at the temporary opening								
S6_9475	TPCWAW - Remaining General fill to +4 within the seawall	7d/wk-1	10d	09-Dec-14 08	18-Dec-14 18	-122d	■ TPCWAW - Remaining General fill to +4 within the seawall								
TPCWAW - Diaphragm Wall															
Diaphragm Wall															
S6_9385	Site investigation	7d/wk-1	48d	01-Dec-14 08	21-Jan-15 18	-113d	■ Site investigation								
S6_8660	Install guide wall	7d/wk-1	40d	17-Dec-14 08	28-Jan-15 18	-120d	■ Install guide wall								
S6_8955	Curtain grout along proposed diaphragm wall	7d/wk-1	40d	19-Dec-14 08	30-Jan-15 18	-122d	■ Curtain grout along proposed diaphragm wall								
S6_9382	Set up bentonite silo/plants and equipments	7d/wk-1	30d	19-Dec-14 08	20-Jan-15 18	-112d	■ Set up bentonite silo/plants and equipments								
S6_9345	Diaphragm wall construction (34 panels @ 3 panels/ week)	7d/wk-1	68d	30-Jan-15 08	14-Apr-15 18	-141d	■ Diaphragm wall construction (34 panels @ 3 panels/ week)								
S6_9350	Install shear pins on diaphragm wall	7d/wk-1	40d	14-Mar-15 08	26-Apr-15 18	-133d	■ Install shear pins on diaphragm wall								
Summary Bar															
Actual Level of Effort															
Actual Work															
Remaining Work															
Critical Remaining Work															
◆ Milestone															
4 of 18							China State Construction Engineering (Hong Kong) Ltd								
							Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)								
							WORKS PROGRAMME REV. M								
							Prepared by William Caluza								
							Date 26-Sep-15								
							Revision 1st submission								
							Checked								
							Approved								
							</								

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
S6_9355	Install king posts	7d/wk-1	40d	14-Mar-15 08	26-Apr-15 18	-133d								
S6_9970	Diaphragm Wall Pile test	7d/wk-1	40d	20-Mar-15 08	03-May-15 18	-129d								
S6_9375	Carry out contact/pressure grouting	7d/wk-1	28d	21-Mar-15 08	22-Apr-15 18	-141d								
<b>TPCWAW- ELS Works</b>														
<b>ELS Works</b>														
S6_9360	Install dewatering wells and piezometers	7d/wk-1	20d	30-Mar-15 08	22-Apr-15 18	-141d								
S6_9365	Install inclinometers inside D-wall	7d/wk-1	20d	15-Apr-15 08	05-May-15 18	-141d								
S6_9975	Carry out pumping tests	7d/wk-1	12d	23-Apr-15 08	05-May-15 18	-141d								
S6_9980	1st Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	06-May-15 08	15-May-15 18	-141d								
S6_9260	Submit pumping test report	7d/wk-1	1d	06-May-15 08	06-May-15 18	-137d								
S6_9895	1st Layer - install lateral support	7d/wk-1	10d	16-May-15 08	26-May-15 18	-141d								
S6_9890	Install vibrating wire strain gauge	7d/wk-1	10d	16-May-15 08	26-May-15 18	-141d								
S6_9895	2nd Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	18-May-15 08	28-May-15 18	-141d								
S6_9000	2nd Layer - install lateral support	7d/wk-1	10d	29-May-15 08	07-Jun-15 18	-141d								
S6_9005	3rd Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	31-May-15 08	09-Jun-15 18	-141d								
S6_9010	3rd Layer - install lateral support	7d/wk-1	10d	10-Jun-15 08	19-Jun-15 18	-141d								
S6_9015	4th Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	12-Jun-15 08	22-Jun-15 18	-141d								
S6_9020	4th Layer - install lateral support	7d/wk-1	10d	23-Jun-15 08	03-Jul-15 18	-141d								
S6_9025	5th Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	25-Jun-15 08	05-Jul-15 18	-141d								
S6_9030	5th Layer - install lateral support	7d/wk-1	10d	27-Jun-15 08	07-Jul-15 18	-141d								
S6_9035	6th Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	08-Jul-15 08	17-Jul-15 18	-141d								
S6_9040	6th Layer - install lateral support	7d/wk-1	10d	18-Jul-15 08	27-Jul-15 18	-69d								
<b>TPCWAW - ROCK EXCAVATION</b>														
S6_6180	Rock excavation to formation	7d/wk-1	112d	18-Jul-15 08	09-Nov-15 18	-141d								
S6_9370	Install tie back anchor to D- Walls (area on west side, near Portion 11)	7d/wk-1	25d	20-Jul-15 08	13-Aug-15 18	-69d								
S6_9415	Install tie back anchor to D- Walls (east area)	7d/wk-1	20d	20-Jul-15 08	08-Aug-15 18	-69d								
S6_9055	Provide Access to WDII Contractor for demolition of bulkhead at Portion 11	7d/wk-2	0d		10-Nov-15 18	-133d								
<b>TPCWAW- CCT RC Structure</b>														
<b>TPCWAW - CCT / OHVD</b>														

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

5 of 18

Prepared by William Caluza

Revision

1st submission

Date

26-Sep...

Checked

Approved

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
S6_9070	TPCWAW - Construct tunnel base slab	7d/wk-1	50d	23-Oct-15 08	11-Dec-15 18	-141d						TPCWAW - Construct tunnel base slab		
S6_9075	TPCWAW - Construct tunnel wall + OHVD + roof slab	7d/wk-1	80d	13-Nov-15 08	02-Feb-16 18	-141d						TPCWAW - Construct tunnel wall + OHVD + roof slab		
S6_9077	TPCWAW - external waterproofing on top of completed CCT box (incl. screeding)	7d/wk-1	26d	03-Feb-16 08	28-Feb-16 18	-120d						TPCWAW - external waterproofing on top of completed CCT box (incl. screeding)		
S6_9078	TPCWAW King post load transfer	7d/wk-1	26d	03-Feb-16 08	28-Feb-16 18	-120d						TPCWAW King post load transfer		
TPCWAW - Removal of Temporary Reclamation														
Removal of Temporary Reclamation														
S6_9140	Backfilling/Removal of ELS/ Reinforcement activities	7d/wk-1	30d	17-Feb-16 08	17-Mar-16 18	-120d						Backfilling/Removal of ELS/ Reinforcement activities		
S6_9105	Remove general fill seawall block (concurrent activities)	7d/wk-1	25d	05-Mar-16 08	30-Mar-16 18	-120d						Remove general fill seawall block (concurrent activities)		
S6_9120	Saw cut diaphragm wall	7d/wk-1	65d	21-Mar-16 08	23-May-16 18	-120d						Saw cut diaphragm wall		
S6_7550	Completion of Section 6 - (KD11), above - 20mPD	7d/wk-2	0d		23-May-16 18	-121d						Completion of Section 6 - (KD11), above - 20mPD		
TPCWAW - Cable Trough/ Maintenance Walkway														
S6_9085	TPCWAW - Cable Trough (access through temp. opening at Portion 19)	7d/wk-2	24d	02-Mar-16 08	25-Mar-16 18	-144d						TPCWAW - Cable Trough (access through temp. opening at Portion 19)		
S6_9135	Completion of Section 5 - TPCWAW Area (KD10), below -20mPD	7d/wk-2	0d		25-Mar-16 18	-144d						Completion of Section 5 - TPCWAW Area (KD10), below -20mPD		
Works in Wan Chai PCWA (Portion 11)														
Initial Works & Utilities Works														
S4_2810	Installation of Hoarding	7d/wk-1	24d	05-May-14 08 A	17-Oct-14 18	-58d						Installation of Hoarding		
S4_2720	Remove existing rock mound	7d/wk-1	24d	21-Oct-14 08	13-Nov-14 18	-61d						Remove existing rock mound		
S4_2750	Carry out Site Investigation for BW1/BW2	7d/wk-1	12d	21-Oct-14 08	01-Nov-14 18	-61d						Carry out Site Investigation for BW1/BW2		
S4_2755	BW1/BW2 Engineers confirmation of provisional Barrettes	7d/wk-1	0d		07-Nov-14 18	-61d						BW1/BW2 Engineers confirmation of provisional Barrettes		
Allow Access to WDI														
S4_2785	Complete Section 4 - Portion 11 (KD9)	7d/wk-2	0d		10-Nov-15 18	-132d						Complete Section 4 - Portion 11 (KD9)		
S4_2775	Return Portion 11 to WDI	7d/wk-1	0d		10-Nov-15 18	-129d						Return Portion 11 to WDI		
Works for Mined Tunnel (Portion 16, 17, 18)														
SR8 (Tunnel Excavation + Lining)														
From West (TPCWAE)														
Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)														
A8676	SR8 Heading Excavation From West, CH 4095- 4107 = 8m @2d/m	7d/wk-1a	16d	03-Sep-14 08 A	28-Sep-14 18	164d						SR8 Heading Excavation From West, CH 4095- 4107 = 8m @2d/m		
Bench Excavation (1.5d-2d/m, 20m separation with heading)														
A8700	SR8 Bench Excavation From West, CH 4055- 4065 = 10m	7d/wk-1a	20d	08-Sep-14 08 A	24-Sep-14 18	148d						SR8 Bench Excavation From West, CH 4055- 4065 = 10m		
Summary Bar														
Actual Level of Effort														
Actual Work														
Remaining Work														
Critical Remaining Work														
Milestone														
Prepared by William Caluza														
Date	Revision	Checked	Approved											
26-Sep-15	1st submission													
China State Construction Engineering (Hong Kong) Ltd														
Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)														
WORKS PROGRAMME REV. M														
CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.														

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016				
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
A8705	SR8 Bench Excavation From West, CH 4085- 4075 = 10m	7d/wk-1a	20d	25-Sep-14 08	15-Oct-14 18	148d									
A8685	SR8 Bench Excavation From West, CH 4075- 4085 = 10m	7d/wk-1a	20d	16-Oct-14 08	04-Nov-14 18	148d									
A8680	SR8 Bench Excavation From West, CH 4085- 4095 = 10m	7d/wk-1a	20d	05-Nov-14 08	24-Nov-14 18	148d									
A8725	SR8 Bench Excavation From West, CH 4095- 4100 = 5m	7d/wk-1a	10d	25-Nov-14 08	04-Dec-14 18	148d									
From East (TS4)															
Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)															
A8495	SR8 Heading Excavation From East CH 4115- 4107 = 8m @2d/m	7d/wk-1a	16d	15-Sep-14 08 A	28-Sep-14 18	10d									
Bench Excavation (1.5d/m, 20m separation with heading)															
A8455	SR8 Bench Excavation From East, CH 4147.5- 4135 = 12.5m	7d/wk-1a	19d	20-Sep-14 08	09-Oct-14 18	0d									
A8470	SR8 Bench Excavation From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	10-Oct-14 08	24-Oct-14 18	0d									
A8460	SR8 Bench Excavation From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	25-Oct-14 08	08-Nov-14 18	0d									
A8465	SR8 Bench Excavation From East, CH 4115- 4100 = 15m	7d/wk-1a	23d	09-Nov-14 08	01-Dec-14 18	0d									
Tunnel Lining Works															
From West - Base Slab (10mbay, 10m separation with benching excavation)															
A8525	SR8, From West, CH 4015 - 4025 = 10mbay, base slab	7d/wk-1a	10d	15-Sep-14 08 A	04-Oct-14 18	137d									
A8530	SR8, From West,CH 4025 - 4035 = 10mbay, base slab	7d/wk-1a	10d	05-Oct-14 08	14-Oct-14 18	163d									
A8535	SR8, From West,CH 4035 - 4045 = 10mbay, base slab	7d/wk-1a	8d	15-Oct-14 08	22-Oct-14 18	165d									
A8540	SR8, From West, CH 4045 - 4055 = 10mbay, base slab	7d/wk-1a	8d	23-Oct-14 08	30-Oct-14 18	165d									
A8545	SR8, From West, CH 4055 - 4065 = 10mbay, base slab	7d/wk-1a	8d	05-Nov-14 08	12-Nov-14 18	160d									
A8550	SR8, From West, CH 4065 - 4075 = 10mbay, base slab	7d/wk-1a	8d	25-Nov-14 08	02-Dec-14 18	148d									
A8555	SR8, From West, CH 4075 - 4085 = 10mbay, base slab	7d/wk-1a	8d	05-Dec-14 08	12-Dec-14 18	148d									
A8560	SR8, From West, CH 4085 - 4095 = 10mbay, base slab	7d/wk-1a	8d	13-Dec-14 08	20-Dec-14 18	150d									
A8561	SR8, From West, CH 4095 - 4105 = 10mbay, base slab	7d/wk-1a	8d	21-Dec-14 08	29-Dec-14 18	152d									
A8562	SR8, From West, CH 4105 - 4115 = 10mbay, base slab	7d/wk-1a	8d	30-Dec-14 08	07-Jan-15 18	154d									
From West - Lining (5mbay, 10m separation with base slab)															
A8575	SR8, From West, CH 3995 - 4000 = 1bay, lining	7d/wk-1a	9d	20-Sep-14 08	28-Sep-14 18	0d									
A8580	SR8, From West, CH 4000 - 4005 = 1bay, lining	7d/wk-1a	9d	05-Oct-14 08	13-Oct-14 18	137d									
A8585	SR8, From West, CH 4005 - 4010 = 1bay, lining	7d/wk-1a	9d	14-Oct-14 08	22-Oct-14 18	137d									
A8590	SR8, From West, CH 4010 - 4015 = 1bay, lining	7d/wk-1a	9d	23-Oct-14 08	31-Oct-14 18	137d									
From East (TS4)															
Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)															
A8495	SR8 Heading Excavation From East CH 4115- 4107 = 8m @2d/m	7d/wk-1a	16d	15-Sep-14 08 A	28-Sep-14 18	10d									
Bench Excavation (1.5d/m, 20m separation with heading)															
A8455	SR8 Bench Excavation From East, CH 4147.5- 4135 = 12.5m	7d/wk-1a	19d	20-Sep-14 08	09-Oct-14 18	0d									
A8470	SR8 Bench Excavation From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	10-Oct-14 08	24-Oct-14 18	0d									
A8460	SR8 Bench Excavation From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	25-Oct-14 08	08-Nov-14 18	0d									
A8465	SR8 Bench Excavation From East, CH 4115- 4100 = 15m	7d/wk-1a	23d	09-Nov-14 08	01-Dec-14 18	0d									
Tunnel Lining Works															
From West - Base Slab (10mbay, 10m separation with benching excavation)															
A8525	SR8, From West, CH 4015 - 4025 = 10mbay, base slab	7d/wk-1a	10d	15-Sep-14 08 A	04-Oct-14 18	137d									
A8530	SR8, From West,CH 4025 - 4035 = 10mbay, base slab	7d/wk-1a	10d	05-Oct-14 08	14-Oct-14 18	163d									
A8535	SR8, From West,CH 4035 - 4045 = 10mbay, base slab	7d/wk-1a	8d	15-Oct-14 08	22-Oct-14 18	165d									
A8540	SR8, From West, CH 4045 - 4055 = 10mbay, base slab	7d/wk-1a	8d	23-Oct-14 08	30-Oct-14 18	165d									
A8545	SR8, From West, CH 4055 - 4065 = 10mbay, base slab	7d/wk-1a	8d	05-Nov-14 08	12-Nov-14 18	160d									
A8550	SR8, From West, CH 4065 - 4075 = 10mbay, base slab	7d/wk-1a	8d	25-Nov-14 08	02-Dec-14 18	148d									
A8555	SR8, From West, CH 4075 - 4085 = 10mbay, base slab	7d/wk-1a	8d	05-Dec-14 08	12-Dec-14 18	148d									
A8560	SR8, From West, CH 4085 - 4095 = 10mbay, base slab	7d/wk-1a	8d	13-Dec-14 08	20-Dec-14 18	150d									
A8561	SR8, From West, CH 4095 - 4105 = 10mbay, base slab	7d/wk-1a	8d	21-Dec-14 08	29-Dec-14 18	152d									
A8562	SR8, From West, CH 4105 - 4115 = 10mbay, base slab	7d/wk-1a	8d	30-Dec-14 08	07-Jan-15 18	154d									
From West - Lining (5mbay, 10m separation with base slab)															
A8575	SR8, From West, CH 3995 - 4000 = 1bay, lining	7d/wk-1a	9d	20-Sep-14 08	28-Sep-14 18	0d									
A8580	SR8, From West, CH 4000 - 4005 = 1bay, lining	7d/wk-1a	9d	05-Oct-14 08	13-Oct-14 18	137d									
A8585	SR8, From West, CH 4005 - 4010 = 1bay, lining	7d/wk-1a	9d	14-Oct-14 08	22-Oct-14 18	137d									
A8590	SR8, From West, CH 4010 - 4015 = 1bay, lining	7d/wk-1a	9d	23-Oct-14 08	31-Oct-14 18	137d									

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

7 of 18

Prepared by William Caluza

Date

26-Sep...

1st submission

Revision

Checked

Approved

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD

7 of 18

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Date	Revision	Checked	Approved
28-Sep-14	1st submission		

Prepared by William Caluza



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A8595	SR8, From West, CH 4015 - 4020 = 1bay, lining	7d/wk-1a	9d	01-Nov-14 08	09-Nov-14 18	137d	■ SR8, From West, CH 4015 - 4020 = 1bay, lining							
A8600	SR8, From West, CH 4020 - 4025 = 1bay, lining	7d/wk-1a	9d	10-Nov-14 08	18-Nov-14 18	137d	■ SR8, From West, CH 4020 - 4025 = 1bay, lining							
A8605	SR8, From West, CH 4025 - 4030 = 1bay, lining	7d/wk-1a	5d	19-Nov-14 08	23-Nov-14 18	137d	■ SR8, From West, CH 4025 - 4030 = 1bay, lining							
A8610	SR8, From West, CH 4030 - 4035 = 1bay, lining	7d/wk-1a	5d	24-Nov-14 08	28-Nov-14 18	137d	■ SR8, From West, CH 4030 - 4035 = 1bay, lining							
A8615	SR8, From West, CH 4035 - 4040 = 1bay, lining	7d/wk-1a	5d	29-Nov-14 08	03-Dec-14 18	137d	■ SR8, From West, CH 4035 - 4040 = 1bay, lining							
A8620	SR8, From West, CH 4040 - 4045 = 1bay, lining	7d/wk-1a	5d	04-Dec-14 08	08-Dec-14 18	137d	■ SR8, From West, CH 4040 - 4045 = 1bay, lining							
A8625	SR8, From West, CH 4045 - 4050 = 1bay, lining	7d/wk-1a	5d	09-Dec-14 08	13-Dec-14 18	137d	■ SR8, From West, CH 4045 - 4050 = 1bay, lining							
A8630	SR8, From West, CH 4050 - 4055 = 1bay, lining	7d/wk-1a	5d	14-Dec-14 08	18-Dec-14 18	137d	■ SR8, From West, CH 4050 - 4055 = 1bay, lining							
A8635	SR8, From West, CH 4055 - 4060 = 1bay, lining	7d/wk-1a	5d	19-Dec-14 08	23-Dec-14 18	137d	■ SR8, From West, CH 4055 - 4060 = 1bay, lining							
A8640	SR8, From West, CH 4060 - 4065 = 1bay, lining	7d/wk-1a	5d	24-Dec-14 08	29-Dec-14 18	137d	■ SR8, From West, CH 4060 - 4065 = 1bay, lining							
A8645	SR8, From West, CH 4065 - 4070 = 1bay, lining	7d/wk-1a	5d	30-Dec-14 08	04-Jan-15 18	137d	■ SR8, From West, CH 4065 - 4070 = 1bay, lining							
A8647	SR8, From West, CH 4070 - 4075 = 1bay, lining	7d/wk-1a	5d	05-Jan-15 08	09-Jan-15 18	137d	■ SR8, From West, CH 4070 - 4075 = 1bay, lining							
A8648	SR8, From West, CH 4075 - 4080 = 1bay, lining	7d/wk-1a	5d	10-Jan-15 08	14-Jan-15 18	137d	■ SR8, From West, CH 4075 - 4080 = 1bay, lining							
A8649	SR8, From West, CH 4080 - 4085 = 1bay, lining	7d/wk-1a	5d	15-Jan-15 08	19-Jan-15 18	137d	■ SR8, From West, CH 4080 - 4085 = 1bay, lining							
A8651	SR8, From West, CH 4085 - 4090 = 1bay, lining	7d/wk-1a	5d	20-Jan-15 08	24-Jan-15 18	137d	■ SR8, From West, CH 4085 - 4090 = 1bay, lining							
A8652	SR8, From West, CH 4090 - 4095 = 1bay, lining	7d/wk-1a	5d	25-Jan-15 08	29-Jan-15 18	137d	■ SR8, From West, CH 4090 - 4095 = 1bay, lining							
A8653	SR8, From West, CH 4095 - 4100 = 1bay, lining	7d/wk-1a	5d	30-Jan-15 08	03-Feb-15 18	137d	■ SR8, From West, CH 4095 - 4100 = 1bay, lining							
A8654	SR8, From West, CH 4100 - 4105 = 1bay, lining	7d/wk-1a	5d	04-Feb-15 08	08-Feb-15 18	137d	■ SR8, From West, CH 4100 - 4105 = 1bay, lining							
From East - Base Slab (10mbay, 10m separation with benching excavation)														
A9775	SR8 From East, CH 4149.5 - 4145 = 4.5m, base slab	7d/wk-1a	8d	02-Dec-14 08	09-Dec-14 18	0d	■ SR8 From East, CH 4149.5 - 4145 = 4.5m, base slab							
A9780	SR8 From East, CH 4145 - 4135 = 10mbay, base slab	7d/wk-1a	8d	10-Dec-14 08	17-Dec-14 18	0d	■ SR8 From East, CH 4145 - 4135 = 10mbay, base slab							
A9785	SR8 From East, CH 4135 - 4125 = 10mbay, base slab	7d/wk-1a	8d	18-Dec-14 08	26-Dec-14 18	8d	■ SR8 From East, CH 4135 - 4125 = 10mbay, base slab							
A9786	SR8 From East, CH 4125 - 4115 = 10mbay, base slab	7d/wk-1a	8d	27-Dec-14 08	04-Jan-15 18	10d	■ SR8 From East, CH 4125 - 4115 = 10mbay, base slab							
From East - Lining (5mbay, 10m separation with base slab)														
A9820	From East, SR8 CH 4149.5 - 4145 = 4.5m, 1 bay, lining	7d/wk-1a	5d	18-Dec-14 08	22-Dec-14 18	0d	■ From East, SR8 CH 4149.5 - 4145 = 4.5m, 1 bay, lining							
A9815	From East, SR8 CH 4145 - 4140 = 1bay, lining	7d/wk-1a	5d	23-Dec-14 08	28-Dec-14 18	6d	■ From East, SR8 CH 4145 - 4140 = 1bay, lining							
A9810	From East, SR8 CH 4140 - 4135 = 1bay, lining	7d/wk-1a	5d	29-Dec-14 08	03-Jan-15 18	6d	■ From East, SR8 CH 4140 - 4135 = 1bay, lining							
A9805	From East, SR8 CH 4135 - 4130 = 1bay, lining	7d/wk-1a	5d	04-Jan-15 08	08-Jan-15 18	6d	■ From East, SR8 CH 4135 - 4130 = 1bay, lining							

<div> <div>Summary Bar</div> <div> <div>Actual Level of Effort</div> <div>Actual Work</div> <div>Remaining Work</div> <div>Critical Remaining Work</div> <div>Milestone</div> </div> </div>		<div> <div>18 of 18</div> <div>China State Construction Engineering (Hong Kong) Ltd</div> <div>Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel / Causeway Bay Typhoon Shelter Section)</div> <div>WORKS PROGRAMME REV. M</div> </div>				<div> <div>Prepared by William Caluza</div> <div> <div>Date</div> <div>26-Sep...</div> <div>1st submission</div> </div> <div> <div>Revision</div> <div></div> </div> <div> <div>Checked</div> <div></div> </div> <div> <div>Approved</div> <div></div> </div> </div>				<div> <div>中國建築工程(香港)有限公司</div> <div>CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.</div> </div>	
---	--	---	--	--	--	--	--	--	--	---	--

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A9870	From East, SR8 CH 4130 - 4125 = 1bay, lining	7d/wk-1a	5d	09-Jan-15 08	13-Jan-15 18	6d								
A9880	From East, SR8 CH 4125 - 4120 = 1bay, lining	7d/wk-1a	5d	14-Jan-15 08	18-Jan-15 18	143d								
A9860	From East, SR8 CH 4120 - 4115 = 1bay, lining	7d/wk-1a	5d	19-Jan-15 08	23-Jan-15 18	143d								
A9855	From East, SR8 CH 4115 - 4110 = 1bay, lining	7d/wk-1a	5d	24-Jan-15 08	28-Jan-15 18	143d								
A9850	From East, SR8 CH 4110 - 4105 = 1bay, lining	7d/wk-1a	5d	29-Jan-15 08	02-Feb-15 18	143d								
	OHVD(10mbay) / Utility Trough													
A8570	SR8 Tunnel OHVD and utility trough =, 167= 17 bays @ 10mbay @ 7dbay	7d/wk-1a	120d	09-Feb-15 08	13-Jun-15 18	137d								
	EB Outer Tunnel Excavation													
	From West (TPCVAE)													
	Outer Bench Excavation (1.5d - 2d/m, 20m separation with heading)													
A9550	EB, Outer Bench From West, CH 4035- 4045 = 10m	7d/wk-1a	30d	07-Aug-14 08 A	20-Oct-14 18	135d								
A9555	EB, Outer Bench From West, CH 4045- 4055 = 10m (2d/m)	7d/wk-1a	20d	20-Oct-14 08	08-Nov-14 18	135d								
A9560	EB, Outer Bench From West, CH 4055- 4065 = 10m (2d/m)	7d/wk-1a	20d	09-Nov-14 08	28-Nov-14 18	135d								
A9565	EB, Outer Bench From West, CH 4065- 4075 = 10m (2d/m)	7d/wk-1a	20d	29-Nov-14 08	18-Dec-14 18	135d								
A9520	EB, Outer Bench From West, CH 4075- 4085 = 10m (2d/m)	7d/wk-1a	20d	19-Dec-14 08	09-Jan-15 18	135d								
A9545	EB, Outer Bench From West, CH 4085- 4095 = 10m 1.5d/m)	7d/wk-1a	15d	10-Jan-15 08	24-Jan-15 18	135d								
	From East (TS4)													
	Outer Bench Excavation (1.5d-2d/m, 20m separation with heading)													
A9605	EB, Outer Bench From East, CH 4147.5 - 4145 = 2.5m	7d/wk-1a	30d	20-Oct-14 08*	18-Nov-14 18	120d								
A9610	EB, Outer Bench From East, CH 4145- 4135 = 10m (2d/m)	7d/wk-1a	20d	19-Nov-14 08	08-Dec-14 18	120d								
A9615	EB, Outer Bench From East, CH 4135- 4125 = 10m (2d/m)	7d/wk-1a	20d	09-Dec-14 08	29-Dec-14 18	120d								
A9620	EB, Outer Bench From East, CH 4125- 4115 = 10m (2d/m)	7d/wk-1a	20d	30-Dec-14 08	19-Jan-15 18	120d								
A9625	EB, Outer Bench From East, CH 4115- 4105 = 10m (2d/m)	7d/wk-1a	20d	20-Jan-15 08	08-Feb-15 18	120d								
A9630	EB, Outer Bench From East, CH 4105- 4095 = 10m (1.5d/m)	7d/wk-1a	15d	09-Feb-15 08	26-Feb-15 18	120d								
	EB (Inner Tunnel Excavation + Lining)													
	From West (TPCVAE)													
	Inner Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)													
A8805	EB, Inner Heading From West, CH 3992- 4005 = 13m @3d/m	7d/wk-1a	39d	29-Sep-14 08	07-Nov-14 18	6d								
A8815	EB, Inner Heading From West, CH 4005- 4015 = 10m @2d/m	7d/wk-1a	20d	08-Nov-14 08	27-Nov-14 18	6d								
	Summary Bar													
	Actual Level of Effort													
	Actual Work													
	Remaining Work													
	Critical Remaining Work													
	Milestone													

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

9 of 18

Prepared by William Calizza



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016	
							Q4	Q1	Q2	Q3	Q4	Q1
A8820	EB,Inner Heading From West , CH 4015- 4025 = 10m @2d/m	7d/wk-1a	20d	28-Nov-14 08	17-Dec-14 18	0d	■	■	■	■	■	■
A8780	EB,Inner Heading From West, CH 4025- 4035 = 10m @2d/m	7d/wk-1a	20d	18-Dec-14 08	08-Jan-15 18	0d	■	■	■	■	■	■
A8810	EB,Inner Heading From West , CH 4035- 4045 = 10m @2d/m	7d/wk-1a	20d	09-Jan-15 08	28-Jan-15 18	0d	■	■	■	■	■	■
A8785	EB,Inner Heading From West , CH 4045- 4055 = 10m @2d/m	7d/wk-1a	20d	29-Jan-15 08	17-Feb-15 18	0d	■	■	■	■	■	■
A8790	EB,Inner Heading From West, CH 4055- 4065 = 10m @ 2d/m	7d/wk-1a	20d	18-Feb-15 08	12-Mar-15 18	0d	■	■	■	■	■	■
A8795	EB,Inner Heading From West , CH 4065- 4075 = 10m, @ 2d/m	7d/wk-1a	20d	13-Mar-15 08	01-Apr-15 18	0d	■	■	■	■	■	■
A8800	EB,Inner Heading From West, CH 4075- 4085 = 10m @ 2d/m	7d/wk-1a	20d	02-Apr-15 08	22-Apr-15 18	0d	■	■	■	■	■	■
A8825	EB,Inner Heading From West, CH 4085- 4095 = 10m @ 2d/m	7d/wk-1a	20d	23-Apr-15 08	13-May-15 18	0d	■	■	■	■	■	■
Inner Bench Excavation (1.5-2d/m, 20m separation with heading)												
A8765	EB, Inner Bench From West, CH 3992- 4005 = 13m (2d/m)	7d/wk-1a	26d	08-Nov-14 08	03-Dec-14 18	23d	■	■	■	■	■	■
A8770	EB, Inner Bench From West,CH 4005- 4015 = 10m	7d/wk-1a	15d	18-Dec-14 08	03-Jan-15 18	9d	■	■	■	■	■	■
A8775	EB, Inner Bench From West,CH 4015- 4025 = 10m	7d/wk-1a	15d	09-Jan-15 08	23-Jan-15 18	4d	■	■	■	■	■	■
A8735	EB, Inner Bench From West,CH 4025- 4035 = 10m	7d/wk-1a	15d	29-Jan-15 08	12-Feb-15 18	14d	■	■	■	■	■	■
A8740	EB, Inner Bench From West,CH 4035- 4045 = 10m	7d/wk-1a	15d	18-Feb-15 08	07-Mar-15 18	11d	■	■	■	■	■	■
A8745	EB, Inner Bench From West,CH 4045- 4055 = 10m	7d/wk-1a	15d	13-Mar-15 08	27-Mar-15 18	6d	■	■	■	■	■	■
A8750	EB, Inner Bench From West,CH 4055- 4065 = 10m	7d/wk-1a	15d	02-Apr-15 08	17-Apr-15 18	1d	■	■	■	■	■	■
A8755	EB, Inner Bench From West,CH 4065- 4075 = 10m	7d/wk-1a	15d	18-Apr-15 08	03-May-15 18	1d	■	■	■	■	■	■
A8760	EB, Inner Bench From West,CH 4075- 4085 = 10m	7d/wk-1a	15d	05-May-15 08	19-May-15 18	0d	■	■	■	■	■	■
A8761	EB, Inner Bench From West,CH 4085- 4095 = 10m	7d/wk-1a	15d	20-May-15 08	03-Jun-15 18	0d	■	■	■	■	■	■
From East (TS4)												
Inner Heading Excavation (3d/m, 24h/day work shift, 7d/week, no work on statutory holiday)												
A8835	EB,Inner Heading From East, CH 4147.5 to 4145 = 2.5m, @ 3d/m	7d/wk-1a	8d	06-Jan-15 08	13-Jan-15 18	0d	■	■	■	■	■	■
A8850	EB,Inner Heading From East, CH 4145- 4135 = 10m, @ 3d/m	7d/wk-1a	30d	14-Jan-15 08	12-Feb-15 18	0d	■	■	■	■	■	■
A8830	EB,Inner Heading From East, CH 4135- 4125 = 10m @2d/m	7d/wk-1a	20d	13-Feb-15 08	07-Mar-15 18	0d	■	■	■	■	■	■
A8840	EB,Inner Heading From East, CH 4125- 4115 = 10m @2d/m	7d/wk-1a	20d	08-Mar-15 08	27-Mar-15 18	0d	■	■	■	■	■	■
A9910	EB,Inner Heading From East, CH 4115- 4105 = 10m @2d/m	7d/wk-1a	20d	28-Mar-15 08	17-Apr-15 18	0d	■	■	■	■	■	■
A8845	EB,Inner Heading From East, CH 4105- 4095 = 10m @2d/m	7d/wk-1a	20d	18-Apr-15 08	08-May-15 18	0d	■	■	■	■	■	■
Inner Bench Excavation (1.5d-2d/m, 20m separation with heading)												
A8860	EB,Inner Bench From East, CH 4147.5 - 4145 = 2.5m	7d/wk-1a	4d	08-Mar-15 08	11-Mar-15 18	11d	■	■	■	■	■	■
Prepared by William Caluza												
Date							Revision	Checked	Approved			
26-Sep...							1st submission					

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

10 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai Bay Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

中國建築工程(香港)有限公司  
CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.

10 of 18

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016				
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
A8865	EB,Inner Bench From East, CH 4145- 4135 = 10m	7d/wk-1a	15d	12-Mar-15 08	26-Mar-15 18	11d			■	■	■				
A8870	EB,Inner Bench From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	28-Mar-15 08	12-Apr-15 18	10d			■	■	■				
A8855	EB,Inner Bench From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	18-Apr-15 08	03-May-15 18	5d			■	■	■				
A8875	EB,Inner Bench From East, CH 4115- 4105 = 10m	7d/wk-1a	15d	09-May-15 08	23-May-15 18	0d			■	■	■				
A8915	EB,Inner Bench From East, CH 4105- 4095 = 10m	7d/wk-1a	16d	24-May-15 08	06-Jun-15 18	0d			■	■	■				
Tunnel Lining Works															
From West Base Slab (10mbay, 10m separation with benching excavation)															
A8900	EB From West, Base Slab CH 3990 - 3995 = 1 bay	7d/wk-1a	10d	04-Dec-14 08	13-Dec-14 18	33d			■	■	■				
A8890	EB From West, Base Slab CH 3995 - 4005 = 10mbay	7d/wk-1a	10d	04-Jan-15 08	13-Jan-15 18	14d			■	■	■				
A8905	EB From West, Base Slab CH 4005 - 4015 = 10mbay	7d/wk-1a	10d	24-Jan-15 08	02-Feb-15 18	4d			■	■	■				
A8910	EB From West, Base Slab CH 4015 - 4025 = 10mbay	7d/wk-1a	10d	13-Feb-15 08	25-Feb-15 18	14d			■	■	■				
A8915	EB From West, Base Slab CH 4025 - 4035 = 10mbay	7d/wk-1a	10d	08-Mar-15 08	17-Mar-15 18	12d			■	■	■				
A8920	EB From West, Base Slab CH 4035 - 4045 = 10mbay	7d/wk-1a	10d	28-Mar-15 08	07-Apr-15 18	8d			■	■	■				
A8925	EB From West, Base Slab CH 4045 - 4055 = 10mbay	7d/wk-1a	10d	18-Apr-15 08	27-Apr-15 18	4d			■	■	■				
A8930	EB From West, Base Slab CH 4055 - 4065 = 10mbay	7d/wk-1a	10d	04-May-15 08	13-May-15 18	5d			■	■	■				
A8880	EB From West, Base Slab CH 4065 - 4075 = 10mbay	7d/wk-1a	10d	20-May-15 08	29-May-15 18	5d			■	■	■				
A8885	EB From West, Base Slab CH 4075 - 4085 = 10mbay	7d/wk-1a	10d	04-Jun-15 08	13-Jun-15 18	0d			■	■	■				
A8895	EB From West, Base Slab CH 4085 - 4095 = 10mbay	7d/wk-1a	10d	14-Jun-15 08	24-Jun-15 18	0d			■	■	■				
From East Base Slab (10mbay, 10m separation with benching excavation)															
A8905	EB From East, Base Slab CH 4149.5 - 4145 = 4.5m	7d/wk-1a	10d	13-Apr-15 08	22-Apr-15 18	26d			■	■	■				
A9000	EB From East, Base Slab CH 4145 - 4135 = 10mbay	7d/wk-1a	10d	04-May-15 08	13-May-15 18	16d			■	■	■				
A8895	EB From East, Base Slab CH 4135 - 4125 = 10mbay	7d/wk-1a	10d	24-May-15 08	02-Jun-15 18	6d			■	■	■				
A8890	EB From East, Base Slab CH 4125 - 4115 = 10mbay	7d/wk-1a	10d	09-Jun-15 08	19-Jun-15 18	0d			■	■	■				
A8885	EB From East, Base Slab CH 4115 - 4105 = 10mbay	7d/wk-1a	10d	19-Jun-15 08	29-Jun-15 18	0d			■	■	■				
A8880	EB From East, Base Slab CH 4105 - 4095 = 10mbay	7d/wk-1a	10d	30-Jun-15 08	10-Jul-15 18	0d			■	■	■				
Lining (5mbay, 15m separation with base slab)															
A9065	EB From West, Lining CH 3990 - 3995 = 1bay	7d/wk-1a	10d	03-Feb-15 08	12-Feb-15 18	4d			■	■	■				
A9005	EB From West, Lining CH 3995 - 4000 = 1bay	7d/wk-1a	10d	13-Feb-15 08	25-Feb-15 18	4d			■	■	■				
A9090	EB From West, Lining CH 4000 - 4005 = 1bay	7d/wk-1a	10d	26-Feb-15 08	07-Mar-15 18	4d			■	■	■				

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

11 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date

26-Sep...

Revision

1st submission

Checked

Approved

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.

11 of 18

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Date

26-Sep...

1st submission

Revision

Checked

Approved

Prepared by William Caliza

China State Construction Engineering (Hong Kong) Ltd

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3				
A9050	EB From West, Lining CH 4005 - 4010 = 1bay	7d/wk-1a	10d	08-Mar-15 08	17-Mar-15 18	4d		■	EB From West, Lining CH 4005 - 4010 = 1bay					
A9055	EB From West, Lining CH 4010 - 4015 = 1bay	7d/wk-1a	10d	18-Mar-15 08	27-Mar-15 18	4d		■	EB From West, Lining CH 4010 - 4015 = 1bay					
A9060	EB From West, Lining CH 4015 - 4020 = 1bay	7d/wk-1a	10d	28-Mar-15 08	05-Apr-15 18	4d		■	EB From West, Lining CH 4015 - 4020 = 1bay					
A9070	EB From West, Lining CH 4020 - 4025 = 1bay	7d/wk-1a	10d	03-Apr-15 08	13-Apr-15 18	4d		■	EB From West, Lining CH 4020 - 4025 = 1bay					
A9075	EB From West, Lining CH 4025 - 4030 = 1bay	7d/wk-1a	10d	12-Apr-15 08	21-Apr-15 18	4d		■	EB From West, Lining CH 4025 - 4030 = 1bay					
A9080	EB From West, Lining CH 4030 - 4035 = 1bay	7d/wk-1a	10d	20-Apr-15 08	29-Apr-15 18	4d		■	EB From West, Lining CH 4030 - 4035 = 1bay					
A9085	EB From West, Lining CH 4035 - 4040 = 1bay	7d/wk-1a	10d	28-Apr-15 08	08-May-15 18	4d		■	EB From West, Lining CH 4035 - 4040 = 1bay					
A9015	EB From West, Lining CH 4040 - 4045 = 1bay	7d/wk-1a	10d	07-May-15 08	16-May-15 18	4d		■	EB From West, Lining CH 4040 - 4045 = 1bay					
A9020	EB From West, Lining CH 4045 - 4050 = 1bay	7d/wk-1a	10d	15-May-15 08	24-May-15 18	4d		■	EB From West, Lining CH 4045 - 4050 = 1bay					
A9025	EB From West, Lining CH 4050 - 4055 = 1bay	7d/wk-1a	10d	23-May-15 08	01-Jun-15 18	4d		■	EB From West, Lining CH 4050 - 4055 = 1bay					
A9030	EB From West, Lining CH 4055 - 4060 = 1bay	7d/wk-1a	10d	31-May-15 08	09-Jun-15 18	4d		■	EB From West, Lining CH 4055 - 4060 = 1bay					
A9035	EB From West, Lining CH 4060 - 4065 = 1bay	7d/wk-1a	10d	07-Jun-15 08	16-Jun-15 18	4d		■	EB From West, Lining CH 4060 - 4065 = 1bay					
A9040	EB From West, Lining CH 4065 - 4070 = 1bay	7d/wk-1a	10d	14-Jun-15 08	24-Jun-15 18	4d		■	EB From West, Lining CH 4065 - 4070 = 1bay					
A9045	EB From West, Lining CH 4070 - 4075 = 1bay	7d/wk-1a	10d	25-Jun-15 08	05-Jul-15 18	0d		■	EB From West, Lining CH 4070 - 4075 = 1bay					
A8955	EB From West, Lining CH 4075 - 4080 = 1bay	7d/wk-1a	10d	30-Jun-15 08	10-Jul-15 18	0d		■	EB From West, Lining CH 4075 - 4080 = 1bay					
A8960	EB From West, Lining CH 4080 - 4085 = 1bay	7d/wk-1a	5d	11-Jul-15 08	15-Jul-15 18	0d		■	EB From West, Lining CH 4080 - 4085 = 1bay					
A8970	EB From West, Lining CH 4085 - 4090 = 1bay	7d/wk-1a	5d	16-Jul-15 08	20-Jul-15 18	0d		■	EB From West, Lining CH 4085 - 4090 = 1bay					
A8975	EB From West, Lining CH 4090 - 4095 = 1bay	7d/wk-1a	5d	21-Jul-15 08	25-Jul-15 18	0d		■	EB From West, Lining CH 4090 - 4095 = 1bay					
A8980	EB From West, Lining CH 4095 - 4100 = 1bay	7d/wk-1a	5d	26-Jul-15 08	30-Jul-15 18	0d		■	EB From West, Lining CH 4095 - 4100 = 1bay					
A8985	EB From West, Lining CH 4100 - 4105 = 1bay	7d/wk-1a	5d	31-Jul-15 08	04-Aug-15 18	0d		■	EB From West, Lining CH 4100 - 4105 = 1bay					
A8990	EB From West, Lining CH 4105 - 4110 = 1bay	7d/wk-1a	5d	05-Aug-15 08	09-Aug-15 18	0d		■	EB From West, Lining CH 4105 - 4110 = 1bay					
A8995	EB From West, Lining CH 4110 - 4115 = 1bay	7d/wk-1a	5d	10-Aug-15 08	14-Aug-15 18	0d		■	EB From West, Lining CH 4110 - 4115 = 1bay					
A9000	EB From West, Lining CH 4115 - 4120 = 1bay	7d/wk-1a	5d	15-Aug-15 08	19-Aug-15 18	0d		■	EB From West, Lining CH 4115 - 4120 = 1bay					
A9010	EB From West, Lining CH 4120 - 4125 = 1bay	7d/wk-1a	5d	20-Aug-15 08	24-Aug-15 18	0d		■	EB From West, Lining CH 4120 - 4125 = 1bay					
A8965	EB From West, Lining CH 4125 - 4130 = 1bay	7d/wk-1a	5d	25-Aug-15 08	29-Aug-15 18	0d		■	EB From West, Lining CH 4125 - 4130 = 1bay					
A8935	EB From West, Lining CH 4130 - 4135 = 1bay	7d/wk-1a	5d	30-Aug-15 08	03-Sep-15 18	0d		■	EB From West, Lining CH 4130 - 4135 = 1bay					
A8940	EB From West, Lining CH 4135 - 4140 = 1bay	7d/wk-1a	5d	04-Sep-15 08	08-Sep-15 18	0d		■	EB From West, Lining CH 4135 - 4140 = 1bay					
A8945	EB From West, Lining CH 4140 - 4145 = 1bay	7d/wk-1a	5d	09-Sep-15 08	13-Sep-15 18	0d		■	EB From West, Lining CH 4140 - 4145 = 1bay					
A8950	EB From West, Lining CH 4145 - 4149.5 = 4.5m	7d/wk-1a	5d	14-Sep-15 08	18-Sep-15 18	0d		■	EB From West, Lining CH 4145 - 4149.5 = 4.5m					

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

12 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai Bay Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date

28-Sep-15

Revision

1st submission

Checked

Approved

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.

12 of 18

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza		Checked		Approved	
Date	Revision				
28-Sep-15	1st submission				



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
<b>OHVD(10m/bay) / Utility Trough</b>														
A9095	EB From West OHVD and utility trough = 167= 17 bays @ 10m/bay @ 7d/bay	7d/wk-1a	120d	03-Jul-15 08	02-Nov-15 18	0d								
<b>WB Outer Tunnel Excavation</b>														
<b>From West (TPCW4E)</b>														
<b>Outer Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)</b>														
A9651	WB, Outer Heading From West, CH 4085- 4092.5 = 7.5m @ 2d/m	7d/wk-1a	15d	13-Sep-14 08 A	30-Sep-14 18	163d								
<b>Outer Bench Excavation (1.5d-2d/m, 20m separation with heading)</b>														
A9680	WB, Outer Bench From West, CH 4025- 4035 = 10m	7d/wk-1a	15d	12-Oct-14 08	26-Oct-14 18	163d								
A9685	WB, Outer Bench From West, CH 4035- 4045 = 10m	7d/wk-1a	15d	27-Oct-14 08	10-Nov-14 18	163d								
A9670	WB, Outer Bench From West, CH 4045- 4055 = 10m	7d/wk-1a	15d	11-Nov-14 08	25-Nov-14 18	163d								
A9675	WB, Outer Bench From West, CH 4055- 4065 = 10m	7d/wk-1a	15d	26-Nov-14 08	10-Dec-14 18	163d								
A9700	WB, Outer Bench From West, CH 4065- 4075 = 10m	7d/wk-1a	15d	11-Dec-14 08	26-Dec-14 18	163d								
A9701	WB, Outer Bench From West, CH 4075- 4082.5 = 7.5m	7d/wk-1a	15d	27-Dec-14 08	11-Jan-15 18	163d								
<b>From East (TSA)</b>														
<b>Outer Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)</b>														
A9730	WB, Outer Heading From East, CH 4105- 4092.5 = 12.5m @2d/m	7d/wk-1a	25d	30-Aug-14 08 A	30-Sep-14 18	188d								
<b>Outer Bench Excavation (1.5d-2d/m, 20m separation with heading)</b>														
A9740	WB, Outer Bench From East, CH 4136- 4135 = 1m	7d/wk-1a	2d	12-Oct-14 08	13-Oct-14 18	168d								
A9770	WB, Outer Bench From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	14-Oct-14 08	28-Oct-14 18	168d								
A9745	WB, Outer Bench From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	28-Oct-14 08	11-Nov-14 18	168d								
A9750	WB, Outer Bench From East, CH 4115- 4105 = 10m	7d/wk-1a	15d	11-Nov-14 08	25-Nov-14 18	168d								
A9755	WB, Outer Bench From East, CH 4105- 4095 = 10m	7d/wk-1a	15d	26-Nov-14 08	10-Dec-14 18	168d								
A9760	WB, Outer Bench From East, CH 4095- 4082.5 = 12.5m	7d/wk-1a	25d	11-Dec-14 08	06-Jan-15 18	168d								
<b>WB (Inner Tunnel Excavation + Lining)</b>														
<b>From West (TPCW4E)</b>														
<b>Inner Heading Excavation (2-3d/m, 24h/day work shift, 7d/week, no work on statutory holiday)</b>														
A9130	WB, Inner Heading From West, CH 3993- 4005 = 12m @3d/m	7d/wk-1a	50d	25-Sep-14 08	18-Nov-14 18	0d								
A9135	WB, Inner Heading From West, CH 4005- 4015 = 10m @2d/m	7d/wk-1a	20d	19-Nov-14 08	08-Dec-14 18	0d								
A9140	WB, Inner Heading From West, CH 4015- 4025 = 10m @2d/m	7d/wk-1a	20d	09-Dec-14 08	29-Dec-14 18	0d								

13 of 18

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date

Revision

Checked

Approved



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016							
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
A9100	WB,Inner Heading From West, CH 4025-4035 = 10m @2d/m	7d/wk-1a	20d	30-Dec-14 08	19-Jan-15 18	0d												
A9105	WB,Inner Heading From West, CH 4035-4045 = 10m @2d/m	7d/wk-1a	20d	20-Jan-15 08	08-Feb-15 18	0d												
A9110	WB,Inner Heading From West, CH 4045-4055 = 10m @2d/m	7d/wk-1a	20d	09-Feb-15 08	03-Mar-15 18	0d												
A9115	WB,Inner Heading From West, CH 4055-4065 = 10m @ 2d/m	7d/wk-1a	20d	04-Mar-15 08	23-Mar-15 18	0d												
A9120	WB,Inner Heading From West, CH 4065-4075 = 10m, @ 2d/m	7d/wk-1a	20d	24-Mar-15 08	13-Apr-15 18	0d												
A9125	WB,Inner Heading From West, CH 4075-4085 = 10m @ 2d/m	7d/wk-1a	20d	14-Apr-15 08	04-May-15 18	0d												
Inner Bench Excavation (1.5d-2d/m, 20m separation with heading)																		
A9180	WB,Inner Bench From West, CH 3993-4005 = 12m	7d/wk-1a	18d	30-Dec-14 08	17-Jan-15 18	27d												
A9205	WB,Inner Bench From West, CH 4005-4015 = 10m	7d/wk-1a	18d	20-Jan-15 08	03-Feb-15 18	25d												
A9190	WB,Inner Bench From West, CH 4015-4025 = 10m	7d/wk-1a	15d	09-Feb-15 08	26-Feb-15 18	20d												
A9185	WB,Inner Bench From West, CH 4025-4035 = 10m	7d/wk-1a	15d	04-Mar-15 08	18-Mar-15 18	16d												
A9155	WB,Inner Bench From West, CH 4035-4045 = 10m	7d/wk-1a	15d	24-Mar-15 08	08-Apr-15 18	10d												
A9160	WB,Inner Bench From West, CH 4045-4055 = 10m	7d/wk-1a	15d	14-Apr-15 08	28-Apr-15 18	5d												
A9165	WB,Inner Bench From West, CH 4055-4065 = 10m	7d/wk-1a	15d	05-May-15 08	19-May-15 18	0d												
A9170	WB,Inner Bench From West, CH 4065-4075 = 10m	7d/wk-1a	15d	20-May-15 08	03-Jun-15 18	0d												
A9175	WB,Inner Bench From West, CH 4075-4085 = 10m	7d/wk-1a	15d	04-Jun-15 08	18-Jun-15 18	0d												
From East (TS4)																		
Inner Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)																		
A9210	WB,Inner Heading From East, CH 4135-4125 = 10m @2d/m	7d/wk-1a	20d	14-Jan-15 08	02-Feb-15 18	6d												
A9215	WB,Inner Heading From East, CH 4125-4115 = 10m @2d/m	7d/wk-1a	20d	03-Feb-15 08	25-Feb-15 18	6d												
A9230	WB,Inner Heading From East, CH 4115-4105 = 10m @2d/m	7d/wk-1a	20d	26-Feb-15 08	17-Mar-15 18	6d												
A9232	WB,Inner Heading From East, CH 4105-4095 = 10m @2d/m	7d/wk-1a	20d	18-Mar-15 08	07-Apr-15 18	6d												
A9225	WB,Inner Heading From East, CH 4095-4085 = 10m @2d/m	7d/wk-1a	20d	08-Apr-15 08	27-Apr-15 18	6d												
Inner Bench Excavation (1.5d-2d/m, 20m separation with heading)																		
A9235	WB,Inner Bench From East, CH 4135-4125 = 10m	7d/wk-1a	15d	18-Mar-15 08	01-Apr-15 18	16d												
A9240	WB,Inner Bench From East, CH 4125-4115 = 10m	7d/wk-1a	15d	08-Apr-15 08	22-Apr-15 18	11d												
A9245	WB,Inner Bench From East, CH 4115-4105 = 10m	7d/wk-1a	15d	28-Apr-15 08	13-May-15 18	6d												
A9247	WB,Inner Bench From East, CH 4105-4095 = 10m	7d/wk-1a	15d	14-May-15 08	28-May-15 18	6d												
A9250	WB,Inner Bench From East, CH 4095-4085 = 10m	7d/wk-1a	15d	29-May-15 08	12-Jun-15 18	6d												
14 of 18																		
Summary Bar							China State Construction Engineering (Hong Kong) Ltd									Prepared by William Caluza		
Actual Level of Effort							Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel / Causeway Bay Typhoon Shelter Section)									Date		
Actual Work							WORKS PROGRAMME REV. M									26-Sep...		
Remaining Work																1st submission		
Critical Remaining Work																Revision		
Milestone																Checked		
																Approved		

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
<b>Tunnel Lining Works</b>															
<b>From West Base Slab (10mbay, 10m separation with benching excavation)</b>															
A9295	WB From West, Base Slab CH 3990 - 3995 = 5mbay	7d/wk-1a	10d	18-Jan-15 08	27-Jan-15 18	37d									
A9320	WB From West, Base Slab CH 3995 - 4005 = 10mbay	7d/wk-1a	10d	04-Feb-15 08	13-Feb-15 18	30d									
A9255	WB From West, Base Slab CH 4005 - 4015 = 10mbay	7d/wk-1a	10d	27-Feb-15 08	08-Mar-15 18	50d									
A9260	WB From West, Base Slab CH 4015 - 4025 = 10mbay	7d/wk-1a	10d	19-Mar-15 08	28-Mar-15 18	40d									
A9265	WB From West, Base Slab CH 4025 - 4035 = 10mbay	7d/wk-1a	10d	09-Apr-15 08	18-Apr-15 18	30d									
A9300	WB From West, Base Slab CH 4035 - 4045 = 10mbay	7d/wk-1a	10d	29-Apr-15 08	09-May-15 18	20d									
A9325	WB From West, Base Slab CH 4045 - 4055 = 10mbay	7d/wk-1a	10d	20-May-15 08	29-May-15 18	10d									
A9305	WB From West, Base Slab CH 4055 - 4065 = 10mbay	7d/wk-1a	10d	04-Jun-15 08	13-Jun-15 18	5d									
A9310	WB From West, Base Slab CH 4065 - 4075 = 10mbay	7d/wk-1a	10d	19-Jun-15 08	29-Jun-15 18	0d									
A9315	WB From West, Base Slab CH 4075 - 4080 = 5m	7d/wk-1a	10d	30-Jun-15 08	10-Jul-15 18	0d									
<b>From East Base Slab (10mbay, 10m separation with benching excavation)</b>															
A9960	WB From East, Base Slab CH 4135 - 4125 = 10mbay	7d/wk-1a	10d	23-Apr-15 08	03-May-15 18	26d									
A9955	WB From East, Base Slab CH 4125 - 4115 = 10mbay	7d/wk-1a	10d	14-May-15 08	23-May-15 18	16d									
A9950	WB From East, Base Slab CH 4115 - 4105 = 10mbay	7d/wk-1a	10d	29-May-15 08	07-Jun-15 18	11d									
A9945	WB From East, Base Slab CH 4105 - 4095 = 10mbay	7d/wk-1a	10d	13-Jun-15 08	23-Jun-15 18	6d									
A9940	WB From East, Base Slab CH 4095 - 4085 = 10mbay	7d/wk-1a	10d	24-Jun-15 08	04-Jul-15 18	6d									
A9941	WB From East, Base Slab CH 4085 - 4080 = 5m	7d/wk-1a	10d	05-Jul-15 08	14-Jul-15 18	6d									
<b>Lining (5mbay, 10m separation with base slab)</b>															
A9430	WB From West, Lining CH 3990 - 3995 = 1bay	7d/wk-1a	7d	14-Feb-15 08	23-Feb-15 18	30d									
A9470	WB From West, Lining CH 3995 - 4000 = 1bay	7d/wk-1a	7d	24-Feb-15 08	02-Mar-15 18	30d									
A9435	WB From West, Lining CH 4000 - 4005 = 1bay	7d/wk-1a	7d	03-Mar-15 08	09-Mar-15 18	30d									
A9360	WB From West, Lining CH 4005 - 4010 = 1bay	7d/wk-1a	7d	10-Mar-15 08	16-Mar-15 18	30d									
A9365	WB From West, Lining CH 4010 - 4015 = 1bay	7d/wk-1a	7d	17-Mar-15 08	23-Mar-15 18	30d									
A9370	WB From West, Lining CH 4015 - 4020 = 1bay	7d/wk-1a	7d	24-Mar-15 08	30-Mar-15 18	30d									
A9375	WB From West, Lining CH 4020 - 4025 = 1bay	7d/wk-1a	7d	31-Mar-15 08	07-Apr-15 18	30d									
A9380	WB From West, Lining CH 4025 - 4030 = 1bay	7d/wk-1a	7d	08-Apr-15 08	14-Apr-15 18	30d									
A9385	WB From West, Lining CH 4030 - 4035 = 1bay	7d/wk-1a	7d	15-Apr-15 08	21-Apr-15 18	30d									

**Summary Bar**

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

**WORKS PROGRAMME REV. M**

15 of 18

Prepared by William Caliza

Date	Revision	Checked	Approved
26-Sep...	1st submission		

**中國建築工程(香港)有限公司**

CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A9390	WB From West, Lining CH 4035 - 4040 = 1bay	7d/wk-1a	7d	22-Apr-15 08	28-Apr-15 18	30d			WB From West, Lining CH 4035 - 4040 = 1bay					
A9390	WB From West, Lining CH 4040 - 4045 = 1bay	7d/wk-1a	7d	28-Apr-15 08	06-May-15 18	30d			WB From West, Lining CH 4040 - 4045 = 1bay					
A9335	WB From West, Lining CH 4045 - 4050 = 1bay	7d/wk-1a	7d	07-May-15 08	13-May-15 18	30d			WB From West, Lining CH 4045 - 4050 = 1bay					
A9340	WB From West, Lining CH 4050 - 4055 = 1bay	7d/wk-1a	7d	14-May-15 08	20-May-15 18	30d			WB From West, Lining CH 4050 - 4055 = 1bay					
A9345	WB From West, Lining CH 4055 - 4060 = 1bay	7d/wk-1a	7d	21-May-15 08	27-May-15 18	30d			WB From West, Lining CH 4055 - 4060 = 1bay					
A9350	WB From West, Lining CH 4060 - 4065 = 1bay	7d/wk-1a	7d	28-May-15 08	03-Jun-15 18	30d			WB From West, Lining CH 4060 - 4065 = 1bay					
A9355	WB From West, Lining CH 4065 - 4070 = 1bay	7d/wk-1a	5d	04-Jun-15 08	08-Jun-15 18	30d			WB From West, Lining CH 4065 - 4070 = 1bay					
A9415	WB From West, Lining CH 4070 - 4075 = 1bay	7d/wk-1a	5d	11-Jul-15 08	15-Jul-15 18	0d			WB From West, Lining CH 4070 - 4075 = 1bay					
A9475	WB From West, Lining CH 4075 - 4080 = 1bay	7d/wk-1a	5d	16-Jul-15 08	20-Jul-15 18	0d			WB From West, Lining CH 4075 - 4080 = 1bay					
A9440	WB From West, Lining CH 4080 - 4085 = 1bay	7d/wk-1a	5d	21-Jul-15 08	25-Jul-15 18	0d			WB From West, Lining CH 4080 - 4085 = 1bay					
A9445	WB From West, Lining CH 4085 - 4090 = 1bay	7d/wk-1a	5d	26-Jul-15 08	30-Jul-15 18	0d			WB From West, Lining CH 4085 - 4090 = 1bay					
A9450	WB From West, Lining CH 4090 - 4095 = 1bay	7d/wk-1a	5d	31-Jul-15 08	04-Aug-15 18	0d			WB From West, Lining CH 4090 - 4095 = 1bay					
A9455	WB From West, Lining CH 4095 - 4100 = 1bay	7d/wk-1a	5d	05-Aug-15 08	09-Aug-15 18	0d			WB From West, Lining CH 4095 - 4100 = 1bay					
A9420	WB From West, Lining CH 4100 - 4105 = 1bay	7d/wk-1a	5d	10-Aug-15 08	14-Aug-15 18	0d			WB From West, Lining CH 4100 - 4105 = 1bay					
A9425	WB From West, Lining CH 4105 - 4110 = 1bay	7d/wk-1a	5d	15-Aug-15 08	19-Aug-15 18	0d			WB From West, Lining CH 4105 - 4110 = 1bay					
A9460	WB From West, Lining CH 4110 - 4115 = 1bay	7d/wk-1a	5d	20-Aug-15 08	24-Aug-15 18	0d			WB From West, Lining CH 4110 - 4115 = 1bay					
A9465	WB From West, Lining CH 4115 - 4120 = 1bay	7d/wk-1a	5d	25-Aug-15 08	29-Aug-15 18	0d			WB From West, Lining CH 4115 - 4120 = 1bay					
A9395	WB From West, Lining CH 4120 - 4125 = 1bay	7d/wk-1a	5d	30-Aug-15 08	03-Sep-15 18	0d			WB From West, Lining CH 4120 - 4125 = 1bay					
A9400	WB From West, Lining CH 4125 - 4130 = 1bay	7d/wk-1a	5d	04-Sep-15 08	08-Sep-15 18	0d			WB From West, Lining CH 4125 - 4130 = 1bay					
A9405	WB From West, Lining CH 4130 - 4135 = 1bay	7d/wk-1a	5d	09-Sep-15 08	13-Sep-15 18	0d			WB From West, Lining CH 4130 - 4135 = 1bay					
A9410	WB From West, Lining CH 4135 - 4136.5 = 1bay	7d/wk-1a	5d	14-Sep-15 08	18-Sep-15 18	0d			WB From West, Lining CH 4135 - 4136.5 = 1bay					
OHVD(10mbay) / Utility Trough														
A9480	WB From West OHVD and utility trough =, 153= 16 bays @ 10mbay @ 7d/bay	7d/wk-1a	115d	08-Jul-15 08	02-Nov-15 18	0d			WB From West OHVD and utility trough =, 153= 16 bays @ 10mbay @ 7d/bay					
Completion of KD10- Section 5														
A8445	KD10- Section 2: Completion of Mined Tunnel Works (orig. Target KD10- 2 Nov 2015)	7d/wk-2	0d		02-Nov-15 18*	0d			KD10- Section 2: Completion of Mined Tunnel Works (orig. Target KD10- 2 Nov 2015)					
Interface works with other Contracts														
S5_60115	Handover TZ6 to MTR	7d/wk-2	0d		30-Sep-14 18	-249d			Handover TZ6 to MTR					
S6_5283	Handover TZ4 to CWB(T2)	7d/wk-2	0d		10-Nov-14 18	-250d			Handover TZ4 to CWB(T2)					
S6_5275	Provide access to CWB (CC) Contractor- TS1 & TS2	7d/wk-2	0d		21-Nov-14 19*	-85d			Provide access to CWB (CC) Contractor- TS1 & TS2					
Summary Bar														
Actual Level of Effort														
Actual Work														
Remaining Work														
Critical Remaining Work														
Milestone														
16 of 18														
China State Construction Engineering (Hong Kong) Ltd														
Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)														
WORKS PROGRAMME REV. M														
Prepared by William Caluza														
Date														
26-Sep-15, 1st submission														
Revision														
Checked														
Approved														
中國建築工程(香港)有限公司														
CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.														

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
SS_5280	Provide access to CWB (CC) Contractor- TS4, TPCWA, Mined Tunnel	7d/wk-2	0d		31-Mar-18*	-124d							◆ Provide access to CWB (CC) C	
<b>Stage and Section Completion</b>														
KD_5735	KD8 - Completion of Section 3, (1326d)	7d/wk-2	0d		30-Sep-14 18*	-86d	◆ KD8 - Completion of Section 3, (1326d)							
KD_5720	KD5 - Achievement of Stage 5, (1152d)	7d/wk-2	0d		16-Oct-14 18*	-323d	◆ KD5 - Achievement of Stage 5, (1152d)							
KD_5760	KD13 - Completion of Section 7B, (1152d)	7d/wk-2	0d		17-Nov-14 18*	-353d	◆ KD13 - Completion of Section 7B, (1152d)							
KD_5730	KD7 - Completion of Section 2, (1152d)	7d/wk-2	0d		17-Nov-14 18*	-297d	◆ KD7 - Completion of Section 2, (1152d)							
KD_5740	KD9 - Completion of Section 4, (1739d)	7d/wk-2	0d		10-Nov-15 18*	-132d	◆ KD9 - Completion of Section 4, (1739d)							
KD_5745	KD10 - Completion of Section 5, (1863d)	7d/wk-2	0d		25-Mar-16 18	-144d	◆ KD10 - Completion of Section 5, (1863d)							
KD_5750	KD11 - Completion of Section 6, (1949d)	7d/wk-2	0d		23-May-16 18*	-121d	◆ KD11 - Completion of Section 6, (1949d)							
<b>Portion Handover Date</b>														
CD_5685	Portion Handover - Portion IV(4), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion IV(4), KD8 +28							
CD_5680	Portion Handover - Portion V (5), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion V (5), KD8 +28							
CD_5695	Portion Handover - Portion VI (6), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion VI (6), KD8 +28							
CD_5735	Portion Handover - Portion XIIIB (13B), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion XIIIB (13B), KD8 +28							
CD_5790	Portion Handover - Portion XXII (22), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion XXII (22), KD8 +28							
CD_5670	Portion Handover - Portion III (3), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion III (3), KD8 +28							
CD_5720	Portion Handover - Portion XIII A (13A), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XIII A (13A), KD7 +28							
CD_5705	Portion Handover - Portion VIII (8), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion VIII (8), KD7 +28							
CD_5730	Portion Handover - Portion XIV A (14A), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XIV A (14A), KD7 +28							
CD_5740	Portion Handover - Portion XV (15), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XV (15), KD7 +28							
CD_5605	Portion Handover - Portion XXIII (23), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XXIII (23), KD7 +28							
CD_5775	Portion Handover - Portion XVIII (18), KD10 +28	7d/wk-2	0d		30-Nov-15 18*	0d	◆ Portion Handover - Portion XVIII (18), KD10 +28							
CD_5710	Portion Handover - Portion XI (11), KD9 +28	7d/wk-2	0d		27-Dec-15 18*	0d	◆ Portion Handover - Portion XI (11), KD9 +28							
CD_5700	Portion Handover - Portion IX (9), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d	◆ Portion Handover - Portion IX (9), KD10 +28							
CD_5745	Portion Handover - Portion XIV B (14B), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d	◆ Portion Handover - Portion XIV B (14B), KD10 +28							
CD_5755	Portion Handover - Portion XVI (16), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d	◆ Portion Handover - Portion XVI (16), KD10 +28							
CD_5750	Portion Handover - Portion XVII (17), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d	◆ Portion Handover - Portion XVII (17), KD10 +28							
CD_5760	Portion Handover - Portion XIX (19), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d	◆ Portion Handover - Portion XIX (19), KD10 +28							
CD_5780	Portion Handover - Portion XXB (20B), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d	◆ Portion Handover - Portion XXB (20B), KD10 +28							

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

17 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date

Revision

Checked

Approved

28-Sep-18

1st submission

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
CD_5690	Portion Handover - Portion VII (7), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5725	Portion Handover - Portion XII (12), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5715	Portion Handover - Portion X (10), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5785	Portion Handover - Portion XXA (20A), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5795	Portion Handover - Portion XXI (21), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov

16 of 18

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

◆

Milestone

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza			
Date	Revision	Checked	Approved
26-Sep..	1st submission		



中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.
