



**Agreement No. CE 30/2018 (EP)  
Environmental Team for Kai Tak Sports Park –  
Design and Construction**

Monthly EM&A Report for November 2021

December 2021



Home Affairs Bureau  
1/F, Block A, Kai Tak Sports Park  
Site Office, Muk Tai Street,  
Kai Tak, Kowloon

**Agreement No. CE 30/2018 (EP)**  
**Environmental Team for Kai Tak Sports Park –**  
**Design and Construction**

Monthly EM&A Report for November 2021

December 2021





## Environmental Permit No. EP-544/2017

### Kai Tak Sports Park - Investigation

### Independent Environmental Checker Verification


#### Reference Document/Plan

Document/ <del>Plan</del> to be <del>Certified</del> / Verified:	Monthly EM&A Report No. 32 (November 2021)
Date of Report:	10 December 2021
Date received by IEC:	10 December 2021

#### Reference EP Condition

Environmental Permit Condition:	3.4
Three hard copies and one electronic copy of the monthly EM&A Report shall be submitted to the Director within 10 working days after the end of each reporting month. The monthly EM&A Reports shall include a summary of all non-compliance with the recommendations in the approved EIA Report (Register No. AEIAR-204/2017) or this Permit. The submissions shall be certified by the ET Leader and verified by the IEC as complying with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of submission shall be provided upon request by the Director.	

#### IEC Verification

I hereby verify that the above referenced document/ <del>plan</del> complies with the above referenced condition of EP-544/2017.	
	
Ms Mandy To	Date: 13 December 2021
Independent Environmental Checker	



**Environmental Permit No. EP- 544/2017**

**Kai Tak Sports Park – Investigation**

**Environmental Team Leader Certification**

**Reference Document /Plan**

Document/ <del>Plan</del> to be Certified:	Monthly EM&A Report for November 2021
Date of Report:	December 2021
Date received by ETL:	10 December 2021

**Reference EP Condition**

Environmental Permit Condition:	3.4
---------------------------------	-----

Three hard copies and one electronic copy of the monthly EM&A Report shall be submitted to the Director within 10 working days after the end of each reporting month. The monthly EM&A Reports shall include a summary of all non-compliance with the recommendations in the approved EIA Report (Register No. AEIAR-204/2017) or this Permit. The submissions shall be certified by the ET Leader and verified by the IEC as complying with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of submission shall be provided upon request by the Director.

**ETL Certification**

I hereby certify that the above reference document complies with the above referenced condition of EP-544/2017.

Mr Sunny Chan  
Environmental Team Leader

Date: 13 December 2021

# Contents

<b>Executive summary</b>	<b>1</b>
<b>1 Introduction</b>	<b>5</b>
1.1 Background	5
1.2 Project Organisation	6
1.3 Works Area and Construction Programme	6
1.4 Construction Works undertaken during the Reporting Period	7
<b>2 Air Quality Monitoring</b>	<b>8</b>
2.1 Introduction	8
2.2 Monitoring Parameters, Frequency and Duration	8
2.3 Monitoring Locations	8
2.4 Monitoring Action and Limit Levels	8
2.5 Monitoring Schedule for the Reporting Period	9
2.6 Monitoring Equipment	9
2.7 Monitoring Methodology	9
2.8 Monitoring Results	10
2.9 Wind Data	10
<b>3 Noise Monitoring</b>	<b>11</b>
3.1 Introduction	11
3.2 Monitoring Parameters, Frequency and Duration	11
3.3 Monitoring Locations	11
3.4 Action and Limit Levels	12
3.5 Monitoring Schedule for the Reporting Period	12
3.6 Monitoring Equipment	12
3.7 Monitoring Methodology	12
3.8 Monitoring Results	13
<b>4 Environmental Site and Audit</b>	<b>14</b>
4.1 Site Inspection	14
4.2 Advice on the Solid and Liquid Waste Management Status	16
4.3 Environmental Licenses and Permits	16
4.4 Implementation Status of Environmental Mitigation Measures	16
4.5 Summary of Exceedance of the Environmental Quality Performance Limit	16
4.6 Summary of Complaints, Notification of Summons and Successful Prosecution	16
<b>5 Future Key Issues</b>	<b>19</b>
5.1 Construction Programme for the Coming Months	19

5.2	Environmental Site Inspection and Monitoring Schedule for the Next Reporting Period	19
<b>6</b>	<b>Conclusions</b>	<b>20</b>
6.1	Conclusions	20

## Figures

Figure 2.1: Location of Air Quality Monitoring Stations

Figure 3.1: Location of Noise Monitoring Stations

## Appendices

Appendix A. Project Organization for Environmental Works

Appendix B. Location of Works Areas

Appendix C. Construction Programme

Appendix D. Event and Action Plan

Appendix E. Environmental Site Inspection and Monitoring Schedule

Appendix F. Calibration Certificates

Appendix G. Monitoring Data and Graphical Plots (Air Quality and Noise)

Appendix H. Wind Data

Appendix I. Waste Flow Table

Appendix J. Environmental Licences and Permits

Appendix K. Environmental Mitigation Measures Implementation Status

Appendix L. Statistics on Environmental Complaints, Notification of Summons and Successful Prosecutions

## Tables

Table 1.1:	Contact Information of Key Personnel	6
Table 2.1:	Air Quality Monitoring Parameters, Frequency and Duration	8
Table 2.2:	Construction Dust Monitoring Locations	8
Table 2.3:	Action and Limit Levels for 1-hour TSP	9
Table 2.4:	1-hour TSP Monitoring Equipment	9
Table 2.5:	Summary of 1-hour TSP Monitoring Results During the Reporting Period	10
Table 3.1:	Noise Monitoring Parameters, Frequency and Duration	11
Table 3.2:	Construction Noise Monitoring Locations	11
Table 3.3:	Action and Limit Level for Construction Noise	12
Table 3.4:	Noise Monitoring Equipment	12
Table 3.5:	Summary of Construction Noise Monitoring Results During the Reporting Period	13
Table 4.1:	Summary of Site Inspections and Recommendations	15
Table 5.1:	Construction Activities for the Next Reporting Period	19
Table D.1:	Event and Action Plan for Construction Air Quality (Action Level)	
Table D.2:	Event and Action Plan for Construction Air Quality (Limit Level)	
Table D.3:	Event and Action Plan for Construction Noise	
Table E.1:	Site Inspection and Monitoring Schedule for November 2021	



Table E.2: Tentative Site Inspection and Monitoring Schedule for December 2021

Table J.1: Summary of Environmental Licences and Permits Status (KTSP)

Table J.2: Summary of Environmental Licences and Permits Status (H/O Development)

Table L.1: Statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions

# Executive summary

The Project – hereby meaning the Designated Project (Items O.6 and O.7 Part I, Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO)), comprising the “Kai Tak Sports Park” (KTSP) project and the Hotel and Office (H/O) Development of NKIL 6607 adjoining the KTSP – is located in the Kai Tak Development (KTD) area in Kowloon.

An EIA Report for the Project (Register No. AEIAR-204/2017) was approved by the Environmental Protection Department (EPD) on 6 January 2017. The current Environmental Permit (EP) for the Project, namely No. EP-544/2017, was issued on 8 September 2017. These documents are available through the EIA Ordinance Register. The Project construction works commenced on 8 April 2019.

In February 2019, Mott MacDonald Hong Kong Limited was appointed by the Home Affairs Bureau (HAB) as the Environmental Team (ET) to implement the Environmental Monitoring & Audit (EM&A) programme for the construction phase and first year of operation of the Project in accordance with the approved EM&A Manual.

This is the 32<sup>nd</sup> Monthly EM&A Report for the construction phase of the Project which summaries findings of the EM&A programme during the reporting period from 1 to 30 November 2021.

## Key Construction Works in the Reporting Period

A summary of construction activities undertaken during the reporting period is presented below:

### KTSP

- Rebar fixing;
- Mobilization and lifting;
- Concreting;
- Excavation; and
- Main Stadium truss delivery.

### H/O Development

- Excavation; and
- Concreting.

## Environmental Monitoring and Audit Progress

The monthly EM&A programme was undertaken by ET in accordance with the approved EM&A Manual. A summary of the monitoring activities during the reporting period is presented below:

Activity	Monitoring Locations	Date
Air Quality Monitoring (1-hour TSP)	AMS1, AMS2	3, 9, 15, 19, 25 Nov 2021
Noise Monitoring (L <sub>eq</sub> (30 min))	NMS1, NMS2	3, 9, 15, 25 Nov 2021
Weekly environmental site inspections	-	3, 10, 17, 23 Nov 2021
Landscape and visual site inspections	-	3, 17 Nov 2021

## Breaches of Action and Limit Levels

### Air Quality

There was no breach of Action or Limit Levels for Air Quality (1-hr TSP) during the reporting month.

### Noise

Two noise related complaints were received during the reporting month. Two Action Levels for Noise were triggered during the reporting month.

No exceedance of Limit Level of noise at NMS1 and NMS2 was recorded during the reporting month.

## Complaint Log

There was two complaints in relation to the environmental impact received during the reporting month.

## Summary of Complaints in the Reporting Month

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
1 Nov 2021	31 Oct 2021	- Complaint of noise nuisance arising from the truss delivery operation in nighttime affecting the residents of the Grand Waterfront. - Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit. - Please take necessary measures to minimize the environmental nuisance arising	1. Noise barrier not less than 2m had been provided on site between the truss delivery working area and the Grand Waterfront according to the CNP requirement. 2. Noise insulating fabric implemented on moving trailer during nighttime truss delivery work. 3. The truss delivery works have been scheduled in the daytime as much as practicable to minimise the noise nuisance at nighttime.	8 Nov 2021

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
		from the construction site.	4. Advance notification of nighttime truss delivery work has been issued to nearby residential according to the CNP requirement. 5. Pre work briefing has been provided to ensure the compliance of CNP requirement to minimise potential noise nuisance during the truss delivery.	
19 Nov 2021	12 Nov 2021	- Complaint of noise nuisance arising from the truss delivery operation in late night on 12/11/2021. - Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit. - Please take necessary measures to minimize the environmental nuisance arising from the construction site.	1. Noise barrier not less than 2m had been provided on site between the truss delivery working area and nearby residential area according to the CNP requirement. 2. Noise insulating fabric implemented on moving trailer during nighttime truss delivery work. 3. The truss delivery works have been scheduled in the daytime as much as practicable to minimise the noise nuisance at nighttime. 4. Advance notification of nighttime truss delivery work has been issued to nearby residential according to the CNP requirement. 5. Pre work briefing has been provided to ensure the compliance of CNP requirement to minimise potential noise nuisance during the truss delivery.	23 Nov 2021

**Notifications of Summons and Successful Prosecutions**

There were no notifications of summons or prosecutions received during this reporting period.

## Reporting Changes

There was no reporting change during the reporting period.

## Future Key Issues

The future key issues to be undertaken in the upcoming month are:

### KTSP

- Rebar fixing;
- Mobilization and lifting;
- Concreting;
- Excavation; and
- Main Stadium truss delivery.

### H/O Development

- Excavation; and
- Concreting.

# 1 Introduction

## 1.1 Background

The Project – hereby meaning the Designated Project (Items O.6 and O.7 Part I, Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO)), comprising the “Kai Tak Sports Park” (KTSP) project and the Hotel and Office (H/O) Development of NKIL 6607 adjoining the KTSP – is located in the Kai Tak Development (KTD) area in Kowloon.

The key construction works of the Project include:

### (i) KTSP project

- a. a multi-purpose Main Stadium with a spectator capacity of around 50,000;
- b. a Public Sports Ground, with a spectator capacity of around 5,000;
- c. an Indoor Sports Centre with a multi-purpose main arena with a seating capacity of up to 10,000 and an ancillary sports hall with a seating capacity of 500;
- d. retail and dining outlets with a gross floor area (GFA) of about 57,000 square metres (m<sup>2</sup>), a bowling centre with 40 lanes and a health and wellness centre with about 2,500 m<sup>2</sup> GFA;
- e. more than 8 hectares of public open space including landscaped deck structures across Shing Kai Road, passive amenities and park features, outdoor ball courts; and
- f. ancillary facilities such as car parks, toilets, changing rooms, etc.

### (ii) H/O Development

- g. an office development;
- h. a 300-room hotel with a GFA of about 16,000 m<sup>2</sup>; and
- i. ancillary facilities such as retails, car parks, etc.

In February 2019, Mott MacDonald Hong Kong Limited (MMHK) was commissioned by the Home Affairs Bureau (HAB) under Agreement No. CE 30/2018 (EP) to undertake the Environmental Team (ET) services for carrying out the Environmental Monitoring & Audit (EM&A) programme during the construction phase and first year of operation of the Project in accordance with the approved Environmental Impact Assessment (EIA) Report (Register No.: AEIAR-204/2017), EM&A Manual (including any subsequent amendments) and EP (including any subsequent variations of it and/or any further environmental permit issued under the EIAO). The current EP (No. EP-544/2017) was issued by EPD on 8 September 2017.

This is the 32<sup>nd</sup> Monthly EM&A Report summarising the key findings of the construction phase EM&A programme from 1 to 30 November 2021 (the “reporting period”) and is submitted to fulfil Condition 3.4 of the EP.

## 1.2 Project Organisation

The organisation chart and lines of communication with respect to the on-site environmental management structure of the key personnel are shown in **Appendix A**. The key personnel contact names and numbers are summarized in **Table 1.1**.

**Table 1.1: Contact Information of Key Personnel**

Party	Position	Name	Telephone	Fax
Project Proponent (Home Affairs Bureau)	Project Director (Sports Park)	Edwin Wong	3586 3403	3586 0591
Supervising Officer's Representative (Home Affairs Bureau)	Senior Engineer	Keith Man	3586 3149	3586 0591
Environmental Team (Mott MacDonald Hong Kong Limited)	Environmental Team Leader	Sunny Chan	2828 5962	2827 1823
	Deputy Environmental Team Leader	Henry Leung (till 4 Nov 2021)	2828 5876	2827 1823
		Ken Wong (from 5 Nov 2021)	2828 5757	2827 1823
Independent Environmental Checker (ERM Hong Kong Limited)	Independent Environmental Checker	Mandy To	2271 3000	3015 8052
Contracted Party (Kai Tak Sports Park Limited)	Assistant Contract Manager	Eric Chung	3552 5003	2845 9295
	Environmental Officer	Gary Yim	3552 5013	3552 5099
<b>Hotel and Office Development</b>				
Project Manager (Sanon Limited)	Senior Group Project Director	David Lee	2910 8368	2815 9949
	Project Manager	William Chan	2910 8363	2815 9949
Project Architect (P&T Architects & Engineers Limited)	Project Architect	Patrick Chan	2832 7205	-
Contractor (Hip Hing Construction Co., Ltd.)	Project Manager	Ian Ku	6099 9686	-
24-hour Community Liaison Hotline	-	-	5587 6112	-

## 1.3 Works Area and Construction Programme

The construction works commenced on 8 April 2019. The works area of the Project is shown in **Appendix B**. The Construction Works Programme of the Project is provided in **Appendix C**.

## 1.4 Construction Works undertaken during the Reporting Period

A summary of construction activities undertaken during this reporting period is presented below:

### KTSP

- Rebar fixing;
- Mobilization;
- Concreting;
- Excavation; and
- Main Stadium truss delivery.

### H/O Development

- Excavation; and
- Concreting.



## 2 Air Quality Monitoring

### 2.1 Introduction

In accordance with the EM&A Manual of the Project, baseline 1-hour Total Suspended Particulates (TSP) levels at air quality monitoring stations AMS1 and AMS2 were established. Impact 1-hour TSP monitoring was conducted for at least three times every 6 days.

### 2.2 Monitoring Parameters, Frequency and Duration

**Table 2.1** summarises the monitoring parameters, frequency and duration of impact noise monitoring.

**Table 2.1: Air Quality Monitoring Parameters, Frequency and Duration**

Parameter	Frequency and Duration
1-hour TSP	3 times every six-days

### 2.3 Monitoring Locations

According to the EM&A Manual, a total of five air quality monitoring stations are identified for impact monitoring. Of these, three air sensitive receivers are planned residential use and were not available for baseline monitoring; the same three are also currently not available for impact monitoring.

**Table 2.2** describes the impact air quality monitoring stations and **Figure 2.1** shows their locations.

**Table 2.2: Construction Dust Monitoring Locations**

Monitoring Station	Location	Status
AMS1	Hong Kong Society for the Blind Workshop, Roof Floor	Existing Air Sensitive Receiver
AMS2	Sky Tower, Podium of Tower 7	Existing Air Sensitive Receiver
AMS3	Kai Tak Area 2B Site 4 (2B4) (residential use)	Planned Air Sensitive Receiver
AMS4	Kai Tak Area 1K Site 3 (1K3) (residential use)	Planned Air Sensitive Receiver
AMS5	Kai Tak Area 1L Site 3 (1L3) (residential use)	Planned Air Sensitive Receiver

During the reporting period, monitoring locations AMS1 and AMS2 were set up at the proposed locations for impact monitoring.

Permission on setting up and carrying out impact monitoring works at AMS3, AMS4 and AMS5 will be sought once each respective development is completed and occupied.

### 2.4 Monitoring Action and Limit Levels

The Action and Limit Levels for 1-hr TSP are provided in **Table 2.3**.

**Table 2.3: Action and Limit Levels for 1-hour TSP**

Monitoring Station	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AMS1 – Hong Kong Society for the Blind Workshop, Roof Floor	283	500
AMS2 – Sky Tower, Podium of Tower 7	280	500
AMS3 - Kai Tak Area 2B Site 4 (2B4) (residential use)	287*	500
AMS4 - Kai Tak Area 1K Site 3 (1K3) (residential use)	287*	500
AMS5 - Kai Tak Area 1L Site 3 (1L3) (residential use)	287*	500

\*Remarks: the Action Level for AMS3, AMS4 and AMS5 were derived from an alternative monitoring station AMS3-4-5 during the baseline monitoring.

The event and action plan is provided in **Appendix D**.

If exceedance(s) at these stations is/are recorded by the ET of the Project, it will carry out an investigation and findings will be reported in the monthly EM&A Report.

## 2.5 Monitoring Schedule for the Reporting Period

The schedule for air quality monitoring at AMS1 and AMS2 in the reporting period is presented in **Appendix E**.

## 2.6 Monitoring Equipment

Portable direct reading dust meters were used to carry out the 1-hour TSP monitoring. The brand(s) and model(s) of the equipment used for air quality monitoring stations AMS1 and AMS2 under this Project are given in **Table 2.4**.

**Table 2.4: 1-hour TSP Monitoring Equipment**

Equipment	Brand	Model No.
Portable direct reading dust meter	Sibata Digital Dust Monitor	LD-3B (S/N: 2Z6239, 276017)

## 2.7 Monitoring Methodology

### Field Monitoring

The measuring procedures of the 1-hour TSP dust meter are in accordance with the Manufacturer’s Instruction Manual as follows:

- Turn the power on.
- Close the air collecting opening cover.
- Push the “TIME SETTING” switch to [BG].
- Push “START/STOP” switch to perform background measurement for 6 seconds.
- Turn the knob at SENSI ADJ position to insert the light scattering plate.
- Leave the equipment for 1 minute upon “SPAN CHECK” is indicated in the display.
- Push “START/STOP” switch to perform automatic sensitivity adjustment. This measurement takes 1 minute.
- Pull out the knob and return it to MEASURE position.
- Setting time period of 1 hour for the 1-hour TSP measurement.

- Push “START/STOP” to start the 1-hour TSP measurement.
- Regular checking of the time period setting to ensure monitoring time of 1 hour.

**Maintenance and Calibration**

- The 1-hour dust meter would be checked at 3-month intervals and calibrated at 1-year intervals throughout all stages of the air quality monitoring.
- Calibration records for direct dust meters are given in **Appendix F**.

**2.8 Monitoring Results**

The monitoring results for 1-hour TSP at AMS1 and AMS2 are summarized in **Table 2.5**. Detailed impact air quality monitoring results are presented in **Appendix G**.

**Table 2.5: Summary of 1-hour TSP Monitoring Results During the Reporting Period**

Monitoring Station	Average, $\mu\text{g}/\text{m}^3$	Min, $\mu\text{g}/\text{m}^3$	Max, $\mu\text{g}/\text{m}^3$	Action Level, $\mu\text{g}/\text{m}^3$	Limit Level, $\mu\text{g}/\text{m}^3$
AMS1	36	24	46	283	500
AMS2	42	33	51	280	500

There was no Action and Limit Level exceedance of 1-hr TSP level recorded at station AMS1, and AMS2 by the ET during the reporting period.

**2.9 Wind Data**

Wind data at Kai Tak automatic weather station collected from the Hong Kong Observatory (HKO) were used for the air quality monitoring and they are shown in **Appendix H**. It is considered that the wind data obtained at the existing Kai Tak wind station are representative of the Project area and could be used for undertaking the construction phase baseline and impact air quality monitoring programme for the Project.

The proposed use of the existing wind data from Kai Tak automatic weather station collected from HKO for wind data collection instead of setting up wind monitoring equipment near the monitoring stations was proposed by ET and agreed by IEC in accordance with the requirements as stated in Section 3.4.7 of the EM&A Manual of the Project.

## 3 Noise Monitoring

### 3.1 Introduction

In accordance with the EM&A Manual, impact noise monitoring was conducted at least once per week for each noise monitoring location during the construction phase of the Project.

### 3.2 Monitoring Parameters, Frequency and Duration

**Table 3.1** summarises the monitoring parameters, frequency and duration of impact noise monitoring.

**Table 3.1: Noise Monitoring Parameters, Frequency and Duration**

Parameter	Frequency and Duration
30-minutes measurement at each monitoring station between 0700 and 1900 on normal weekdays (Monday to Saturday). L <sub>eq</sub> , L <sub>10</sub> and L <sub>90</sub> would be recorded.	At least once per week

### 3.3 Monitoring Locations

According to the approved EM&A Manual, a total of seven noise monitoring stations were identified for the impact monitoring locations. Of these, five noise sensitive receivers are planned residential use (NMS1A, NMS2A, NMS3, NMS4 and NMS5) and were not available for baseline monitoring; the same five are also currently not available for impact monitoring.

**Table 3.2** describes the details of the monitoring stations and **Figure 3.1** shows the locations of noise monitoring stations.

**Table 3.2: Construction Noise Monitoring Locations**

Monitoring Station	Location Description	Status
NMS1	Hong Kong Society for the Blind Workshop, Roof Floor	Existing Noise Sensitive Receiver
NMS2	Sky Tower, Podium of Tower 7	Existing Noise Sensitive Receiver
NMS1A	Sung Wong Toi Road Public Housing Site	Planned Noise Sensitive Receiver
NMS2A	Sung Wong Toi Road CDA Site (mixed use)	Planned Noise Sensitive Receiver
NMS3	Kai Tak Area 2B Site 4 (2B4) (residential use)	Planned Noise Sensitive Receiver
NMS4	Kai Tak Area 1K Site 3 (1K3) (residential use)	Planned Noise Sensitive Receiver
NMS5	Kai Tak Area 1L Site 3 (1L3) (residential use)	Planned Noise Sensitive Receiver

During the reporting period, monitoring locations NMS1 and NMS2 were set up at the proposed locations for impact monitoring.

Since NMS1A & NMS2A are planned (i.e. not existing) noise sensitive receivers, noise monitoring should be carried out initially at NMS1 and NMS2 respectively before the population intake of the planned developments. Once the planned developments are completed and occupied, NMS1A shall replace NMS1, while NMS2A shall replace NMS2. It is proposed that

the baseline noise level and Limit Level at NMS1A and NMS2A will be the same as those derived from the baseline monitoring data recorded at NMS1 and NMS2 respectively.

Permission on setting up and carrying out impact monitoring works at NMS3, NMS4 and NMS5 will be sought once each respective development is completed and occupied.

### 3.4 Action and Limit Levels

The Action and Limit Levels for construction noise are defined in **Table 3.3**.

**Table 3.3: Action and Limit Level for Construction Noise**

Monitoring Station	Time Period	Action Level	Limit Level
NMS1 NMS2	0700 – 1900 hours on normal weekdays	When one documented complaint is received	75 dB(A)

The event and action plan is provided in **Appendix D**.

If exceedance(s) at these stations is/are recorded by the ET of the Project, it will carry out an investigation and findings will be reported in the monthly EM&A Report.

### 3.5 Monitoring Schedule for the Reporting Period

The schedule for noise monitoring in the reporting period is presented in **Appendix E**.

### 3.6 Monitoring Equipment

Noise monitoring was performed using sound level meters at each designed monitoring station. The sound level meters deployed comply with the International Electrotechnical Commission Publications (IEC) 651:1979 (Type 1) and 804:1985 (Type 1) specifications. Acoustic calibrator was deployed to check the sound level meters at a known sound pressure level. Brand and model of the equipment used for noise monitoring under this Project is given in **Table 3.4**.

**Table 3.4: Noise Monitoring Equipment**

Equipment	Brand	Model No.
Integrated Sound Level Meter	Rion	NL-52 (serial no. 00131627)
Acoustic Calibrator	LARSON DAVIS	CAL200 (S/N 11334)

### 3.7 Monitoring Methodology

- Façade and Free Field measurements were made at the monitoring locations.
- For Façade measurement, the microphone hear of the head level meter was positioned 1m exterior of the noise sensitive façade and lowered sufficiently so that the building’s external wall acts as a reflecting surface.
- For free field, the microphone of the Sound Level Meter was set at least 1.2 m above the ground.
- A correction of +3dB(A) was made for free field measurement.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
  - frequency weighting: A
  - time weighting: Fast

- time measurement: 30-minute intervals (between 0700-1900 on normal weekdays)
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1 kHz. If the difference in the calibration level before and after measurement was more than 1 dB, the measurement would be considered invalid and repeated after the re-calibration or repair of the equipment.
- During the monitoring period, the  $L_{eq}$ ,  $L_{10}$  and  $L_{90}$  were recorded. In addition, any site observations and noise sources were recorded on a standard record sheet.
- Noise measurements were not made in presence of fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s.

**Maintenance and Calibration**

- The microphone head of the sound level meter and calibrator is cleaned with soft cloth at quarterly intervals.
- The sound level meter and calibrator are sent to the supplier or HOKLAS laboratory to check and calibrate at yearly intervals.
- Calibration records are shown in **Appendix F**.

**3.8 Monitoring Results**

The monitoring results for construction noise are summarized in **Table 3.5**. Detailed impact noise monitoring results and relevant graphical plots are presented in **Appendix G**.

**Table 3.5: Summary of Construction Noise Monitoring Results During the Reporting Period**

Monitoring Station	Measured Noise Level $L_{eq}$ (30 mins), dB(A)			
	Average	Min	Max	Limit Level
NMS1	68	68	69	75
NMS2	69	67	71	75

No noise exceedances were recorded at stations NMS1 and NMS2 by ET during the reporting period.

## 4 Environmental Site and Audit

### 4.1 Site Inspection

Site inspections were carried out by ET on a weekly basis to monitor the implementation of proper environmental pollution control mitigation measures for the Project. Key observations were recorded in the site inspection checklist and passed to the Contracted Party together with the appropriate recommended mitigation measures where necessary. During the reporting period, site inspections were carried out on 3, 10, 17 and 23 November 2021. Joint IEC site inspections were carried out 10 and 23 November 2021.

Bi-weekly landscape and visual site audit was carried out on 3 and 17 November 2021. The landscape and visual audit have been audited by Registered Landscape Architect (RLA). No major observations of landscape and visual impact were identified. The result findings were summarised in **Appendix K**.

Key observations during the site inspections are described in **Table 4.1**.

**Table 4.1: Summary of Site Inspections and Recommendations**

Inspection Date	Key Observations	Recommendations / Actions	Close-Out Date / Status
<b>Kai Tak Sports Park</b>			
3 Nov 2021	A chemical container without drip tray was observed at southern site	The contractor was reminded to provide drip tray for the chemical container.	10 Nov 2021
3 Nov 2021	Dry surface was observed at southern site	The contractor was reminded to provide water spraying to maintain wet surface.	10 Nov 2021
3 Nov 2021	Accumulation of stockpile without covering was observed at southern site	The contractor was reminded to provide covering for the stockpile on site.	10 Nov 2021
10 Nov 2021	Dry haul road was observed at northern site	The contractor was reminded to provide water spraying to maintain wet surface.	17 Nov 2021
10 Nov 2021	Accumulation of construction waste on the ground was observed at northern site	The contractor was reminded to clear the construction waste regularly.	17 Nov 2021
17 Nov 2021	Dry haul road was observed at southern site	The contractor was reminded to provide water spraying to maintain wet surface.	23 Nov 2021
17 Nov 2021	Accumulation of construction materials in the drip tray was observed at southern site	The contractor was reminded to keep the drip tray clear from construction materials.	23 Nov 2021
23 Nov 2021	A generator with faded colour NRMM label was observed at southern site	The contractor was reminded to display new NRMM label for the generator.	1 Dec 2021
23 Nov 2021	Dry haul road was observed at southern site	The contractor was reminded to provide water spraying for the haul road to maintain wet surface.	1 Dec 2021
23 Nov 2021	Stockpile without covering was observed at northern site	The contractor was reminded to provide covering for the stockpile.	1 Dec 2021
<b>Hotel and Office Development</b>			
10 Nov 2021	Dry surface was observed at the working platform.	The contractor was reminded to provide water spraying to maintain wet surface.	17 Nov 2021
23 Nov 2021	Chemical container without drip tray was observed on site.	The contractor was reminded to provide drip tray for the chemical containers.	1 Dec 2021



## 4.2 Advice on the Solid and Liquid Waste Management Status

### KTSP

The Contracted Party was registered as a chemical waste producer for the Project. Construction and demolition (C&D) material sorting was carried out on site. Sufficient numbers of receptacles were provided for general refuse collection and sorting. Excavated inert C&D materials were reused to minimise the disposal of C&D waste to public fill.

The Contracted Party was reminded to maintain on site waste sorting and recording system and maximize reuse / recycling of C&D wastes, whenever these are generated.

### H/O Development

Construction and demolition (C&D) material sorting was carried out on site. Sufficient numbers of receptacles were provided for general refuse collection and sorting. Excavated inert C&D materials were designated for on temporary site storage and collected for the disposal to public fill.

The Contractor was reminded to maintain on site waste sorting and maximize reuse / recycling of C&D wastes, whenever these are generated.

The monthly summary of waste flow table is detailed in [Appendix I](#).

## 4.3 Environmental Licenses and Permits

The valid environmental licenses and permits for the Project during the reporting period are summarized in [Appendix J](#).

## 4.4 Implementation Status of Environmental Mitigation Measures

In response to the site audit findings, the Contracted Party carried out corrective actions.

A summary of the environmental mitigation measures implementation status is presented in [Appendix K](#). Most of the necessary mitigation measures were implemented properly.

## 4.5 Summary of Exceedance of the Environmental Quality Performance Limit

### Air Quality

No Action and Limit Level exceedances of 1-hour TSP level was recorded at AMS1 and AMS2 during the reporting period.

### Noise

Two noise related complaints were received during the reporting month. Two Action Levels for Noise were triggered during the reporting month.

No exceedance of Limit Level of noise at NMS1 and NMS2 was recorded during the reporting month.

## 4.6 Summary of Complaints, Notification of Summons and Successful Prosecution

### Complaints

There was two complaints received in relation to the environmental impact during the reporting month.

## Summary of Complaints in the Reporting Month

Date of Notification from EPD	Date of Complaint	Description of Complaint	Recommendations / Actions	Close-Out Date / Status
1 Nov 2021	31 Oct 2021	<p>- Complaint of noise nuisance arising from the truss delivery operation in nighttime affecting the residents of the Grand Waterfront.</p> <p>- Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit.</p> <p>- Please take necessary measures to minimize the environmental nuisance arising from the construction site.</p>	<ol style="list-style-type: none"> <li>Noise barrier not less than 2m had been provided on site between the truss delivery working area and the Grand Waterfront according to the CNP requirement.</li> <li>Noise insulating fabric implemented on moving trailer during nighttime truss delivery work.</li> <li>The truss delivery works have been scheduled in the daytime as much as practicable to minimise the noise nuisance at nighttime.</li> <li>Advance notification of nighttime truss delivery work has been issued to nearby residential according to the CNP requirement.</li> <li>Pre work briefing has been provided to ensure the compliance of CNP requirement to minimise potential noise nuisance during the truss delivery.</li> </ol>	8 Nov 2021
19 Nov 2021	12 Nov 2021	<p>- Complaint of noise nuisance arising from the truss delivery operation in late night on 12/11/2021.</p> <p>- Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit.</p> <p>- Please take necessary measures to minimize the environmental nuisance arising</p>	<ol style="list-style-type: none"> <li>Noise barrier not less than 2m had been provided on site between the truss delivery working area and nearby residential area according to the CNP requirement.</li> <li>Noise insulating fabric implemented on moving trailer during nighttime truss delivery work.</li> <li>The truss delivery works have been scheduled in the daytime as much as practicable to minimise the noise</li> </ol>	23 Nov 2021

---

from the nuisance at  
construction site. nighttime.  
4. Advance notification of  
nighttime truss  
delivery work has  
been issued to  
nearby residential  
according to the  
CNP requirement.  
5. Pre work briefing  
has been provided  
to ensure the  
compliance of CNP  
requirement to  
minimise potential  
noise nuisance  
during the truss  
delivery.

---

Details of the complaint investigations are shown in **Appendix M**.

#### **Notification of Summons and Successful Prosecution**

No notification of summons or prosecutions was received during the reporting period.

Statistics on notifications of summons and successful prosecutions are summarized in **Appendix L**.

## 5 Future Key Issues

### 5.1 Construction Programme for the Coming Months

As informed by the Contracted Party, the major construction activities for the next reporting period (December 2021) are summarized in **Table 5.1**.

**Table 5.1: Construction Activities for the Next Reporting Period**

Site Area	Description of Activities
<ul style="list-style-type: none"><li>• Kai Tak Sports Park</li></ul>	<ul style="list-style-type: none"><li>• Rebar fixing;</li><li>• Mobilization and lifting;</li><li>• Concreting;</li><li>• Excavation; and</li><li>• Main Stadium truss delivery.</li></ul>
<ul style="list-style-type: none"><li>• Hotel and Office Development</li></ul>	<ul style="list-style-type: none"><li>• Excavation; and</li><li>• Concreting.</li></ul>

### 5.2 Environmental Site Inspection and Monitoring Schedule for the Next Reporting Period

The tentative schedule for weekly site inspection and monitoring for air quality and noise for the next reporting period is provided in **Appendix E**.

## 6 Conclusions

### 6.1 Conclusions

#### General

The construction works for the Project commenced on 8 April 2019.

The ET of the Project has implemented the air quality and noise environmental impact monitoring under the construction phase EM&A programme during the reporting period.

#### Breaches of Action and Limit Levels

##### *Air Quality*

No Action or Limit Level exceedances of 1-hour TSP level was recorded during the reporting period.

##### *Noise*

Two noise related complaints were received during the reporting month. Two Action Levels for Noise were triggered during the reporting month.

No exceedance of Limit Level of noise at NMS1 and NMS2 was recorded during the reporting month.

#### Environmental Site Inspections

Environmental site inspections were carried out four times during the reporting period. Recommendations on remedial actions were given to the Contracted Party for the deficiencies identified during the site inspections.


#### Complaints

There was two complaints received in relation to the environmental impact during the reporting period. Complaint investigations were conducted and mitigation measures were implemented.

#### Notifications of Summons and Successful Prosecutions

There were no notifications of summons or prosecutions received during the reporting period.

# Figures

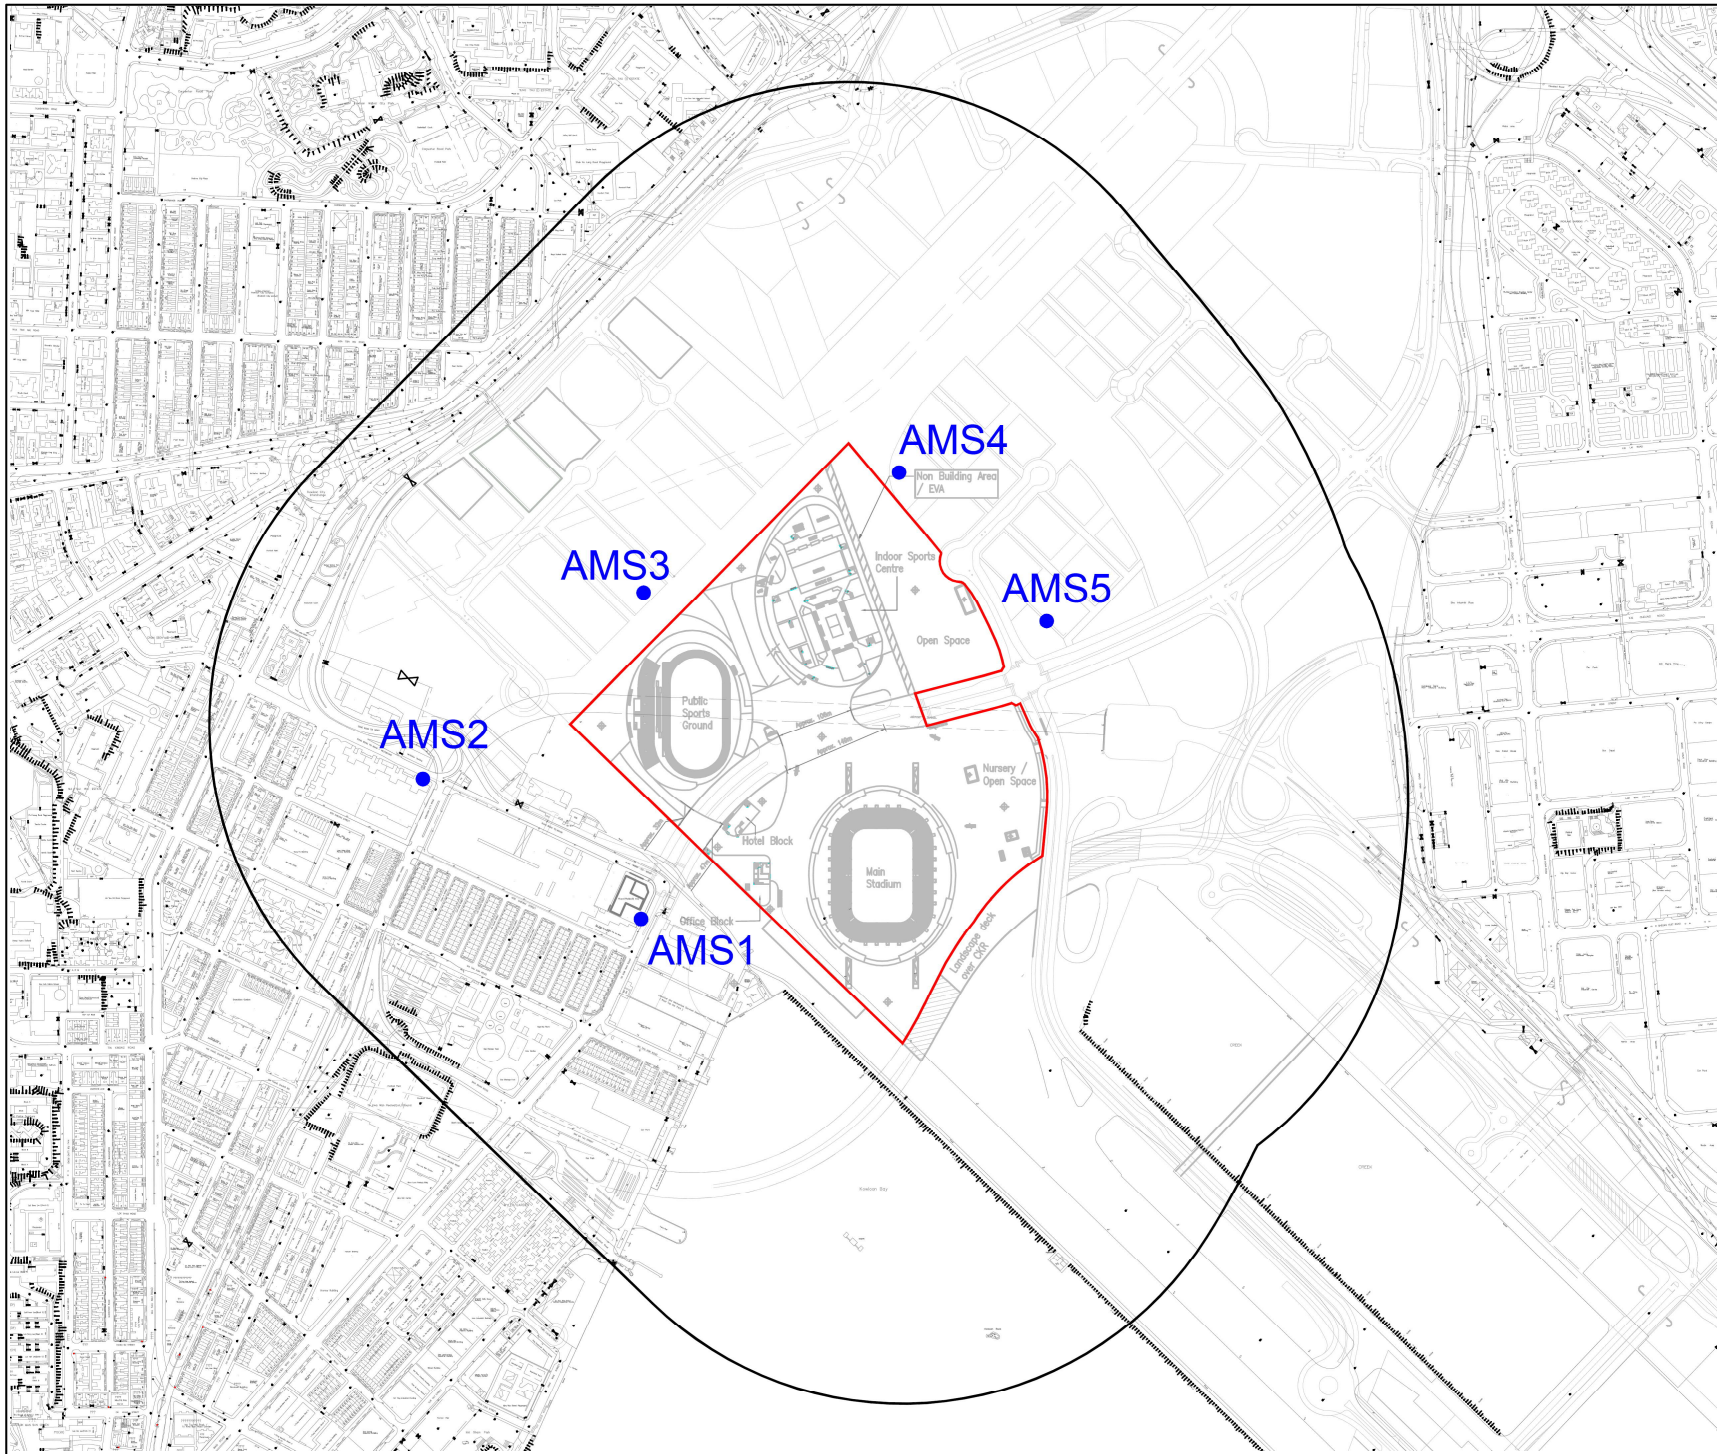

Key Plan

Notes:

1. ALL LEVELS ARE METRES TO PRINCIPAL DATUM (PD) UNLESS NOTED OTHERWISE.
2. ALL CO-ORDINATES REFER TO HONG KONG (1980) METRIC GRID CO-ORDINATES SYSTEM.
3. PIPE AND BOX CULVERT SIZES ARE SHOWN IN MILLIMETERS

Key to symbols:

**LEGEND:**

- Project Site
- 500m from Site Boundary
- AMS1 • Air Monitoring Station 1

Rev	Date	Drawn	Description	Ch'g'd	App'd

**M**  
**MOTT**  
**MACDONALD**


3/F, Mapletree Bay Point  
348 Kowloon Tong Road  
Kowloon, Kowloon  
Hong Kong  
T +852 2828 5757  
F +852 2827 1659  
W mottmac.com

Client

Project

Figure 2.1  
Location of Air Quality Monitoring Stations

Designed		Eng check	
Drawn		Consultation	
Dwg check		Approved	
Scale at A3	Status	Rev	
Drawing Number			

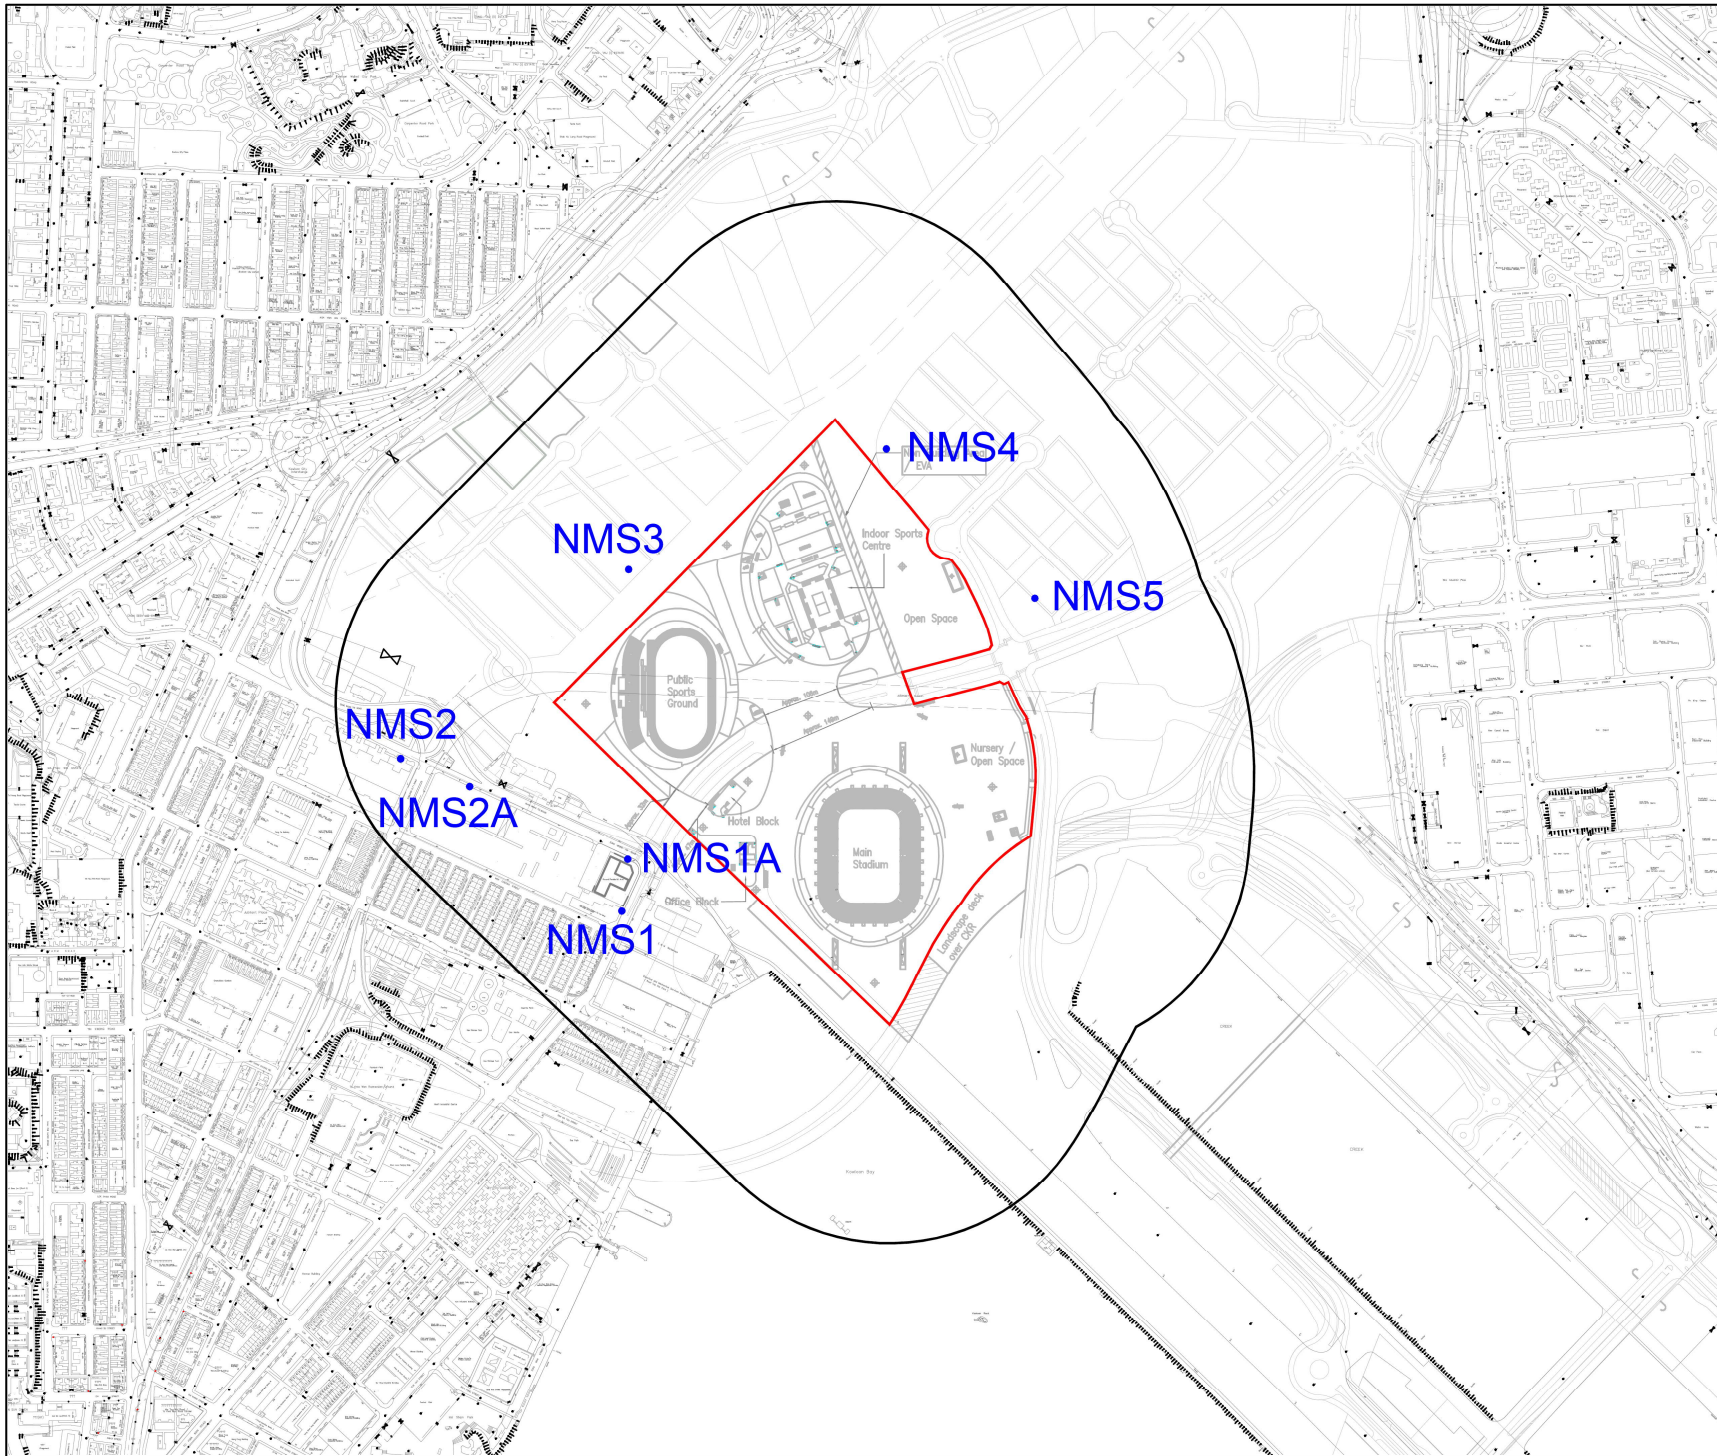

Key Plan

- Notes:
1. ALL LEVELS ARE METRES TO PRINCIPAL DATUM (PD) UNLESS NOTED OTHERWISE.
  2. ALL CO-ORDINATES REFER TO HONG KONG (1980) METRIC GRID CO-ORDINATE SYSTEM.
  3. PIPE AND BOX DIA/VERT SIZES ARE SHOWN IN MILLIMETERS

Key to symbols:

**LEGEND:**

- Project Site
- 300m from Site Boundary
- NMS1 • Construction Noise Monitoring Station 1

Rev	Date	Drawn	Description	Ch'g'd	App'd

**M M**  
**MOTT MACDONALD**

3/F, Mapletree Bay Point  
 348 Kwun Tong Road  
 Kowloon, Kowloon  
 Hong Kong  
 T +852 2828 5757  
 F +852 2827 1650  
 W mottmac.com

Client

Project

Figure 3.1  
 Location of Noise Monitoring Stations


Designed		Eng check	
Drawn		Consultation	
Dwg check		Approved	
Scale at A3	Status		Rev

Drawing Number




# Appendix A. Project Organization for Environmental Works

# Project Organisation for Environmental Works

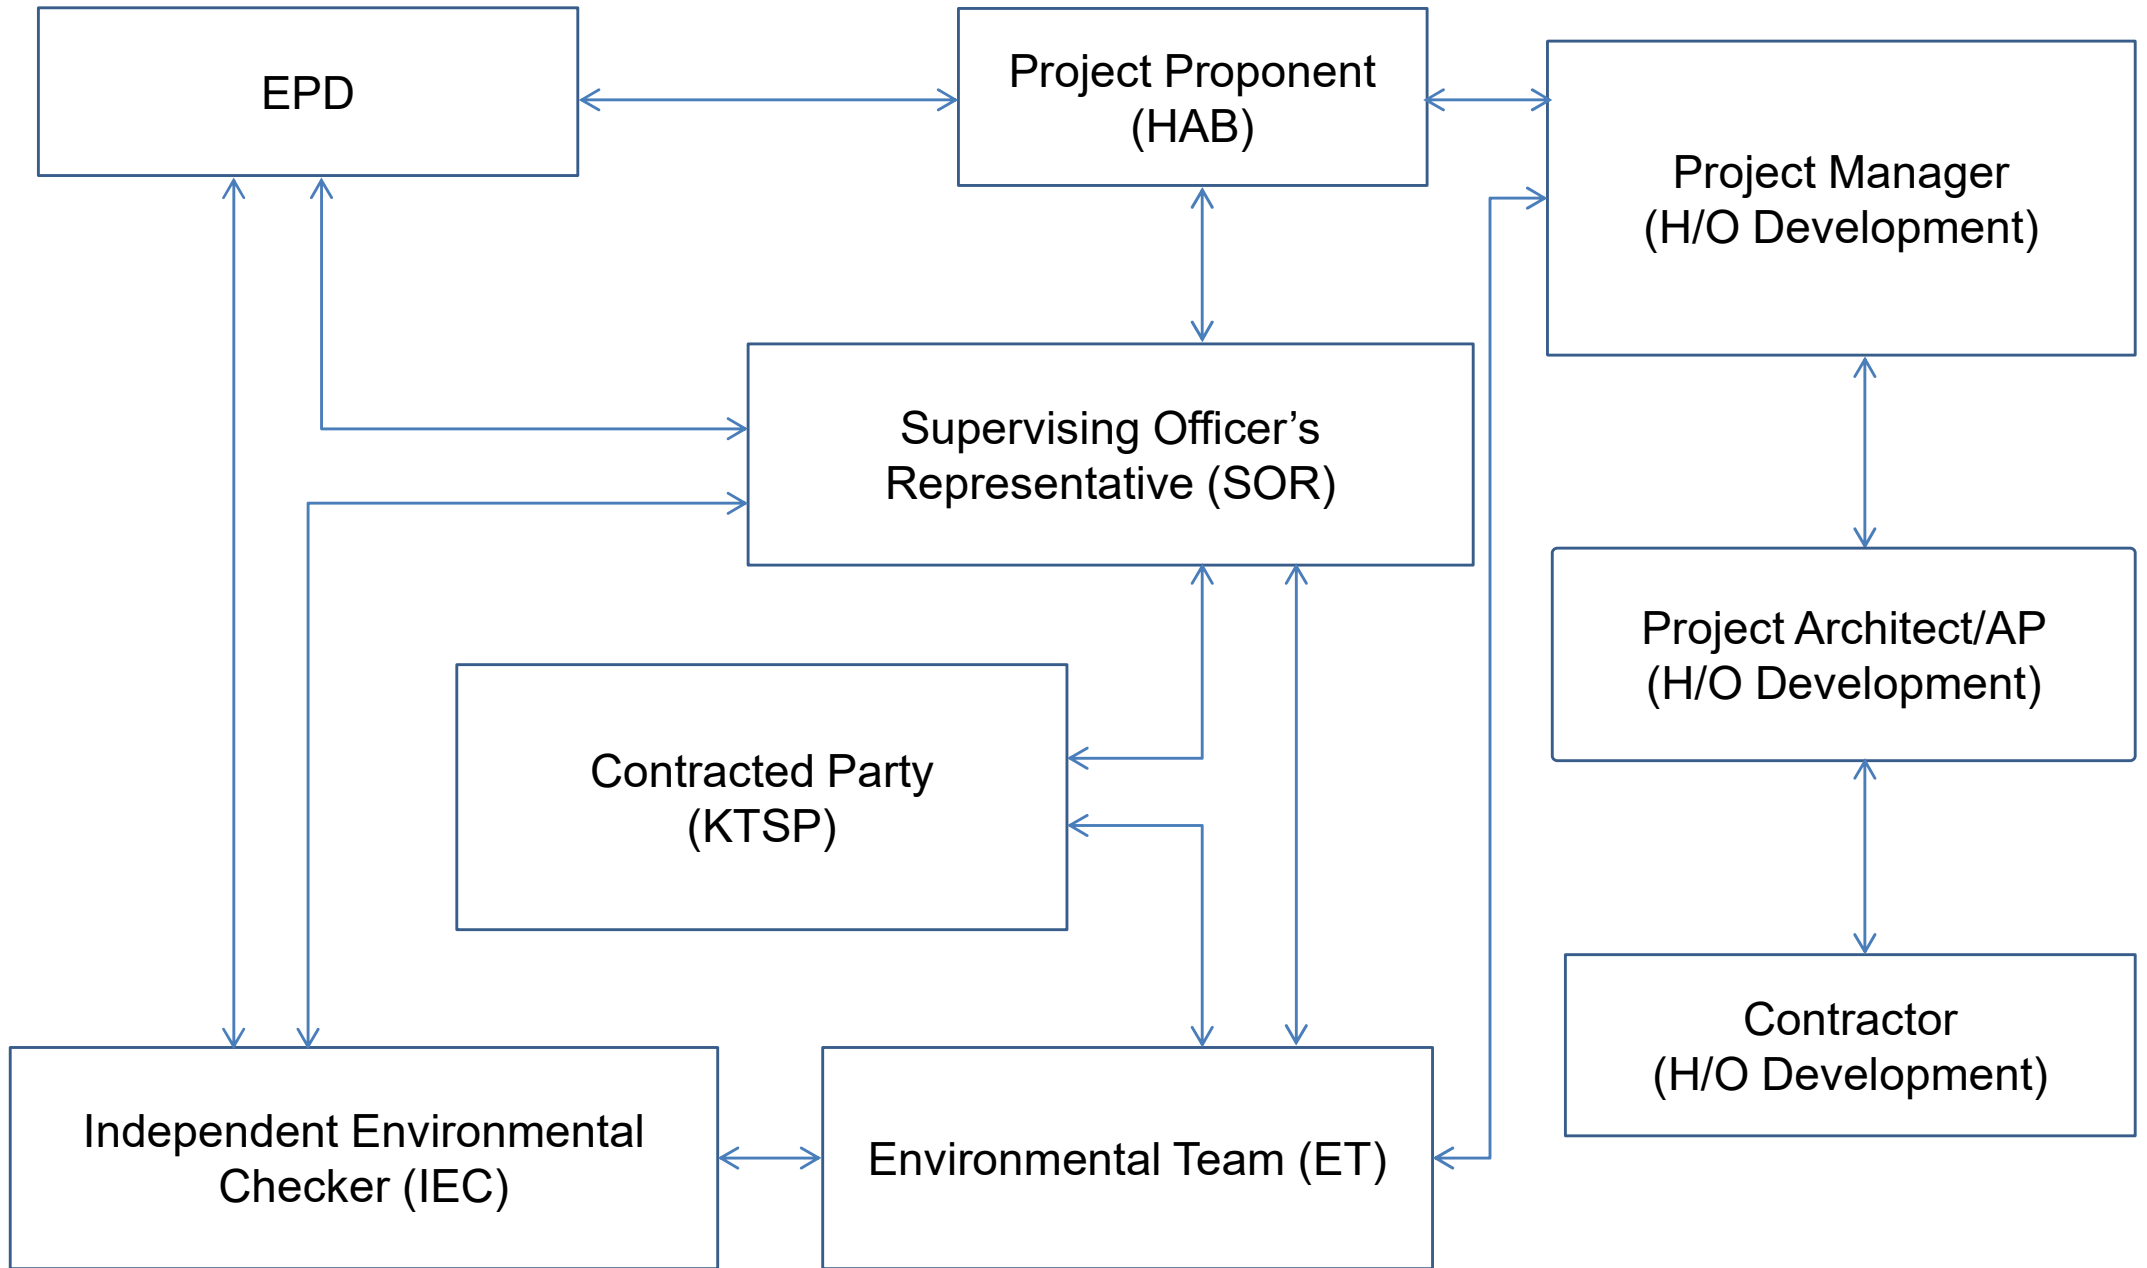

↔ Line of communication

## Appendix B. Location of Works Areas

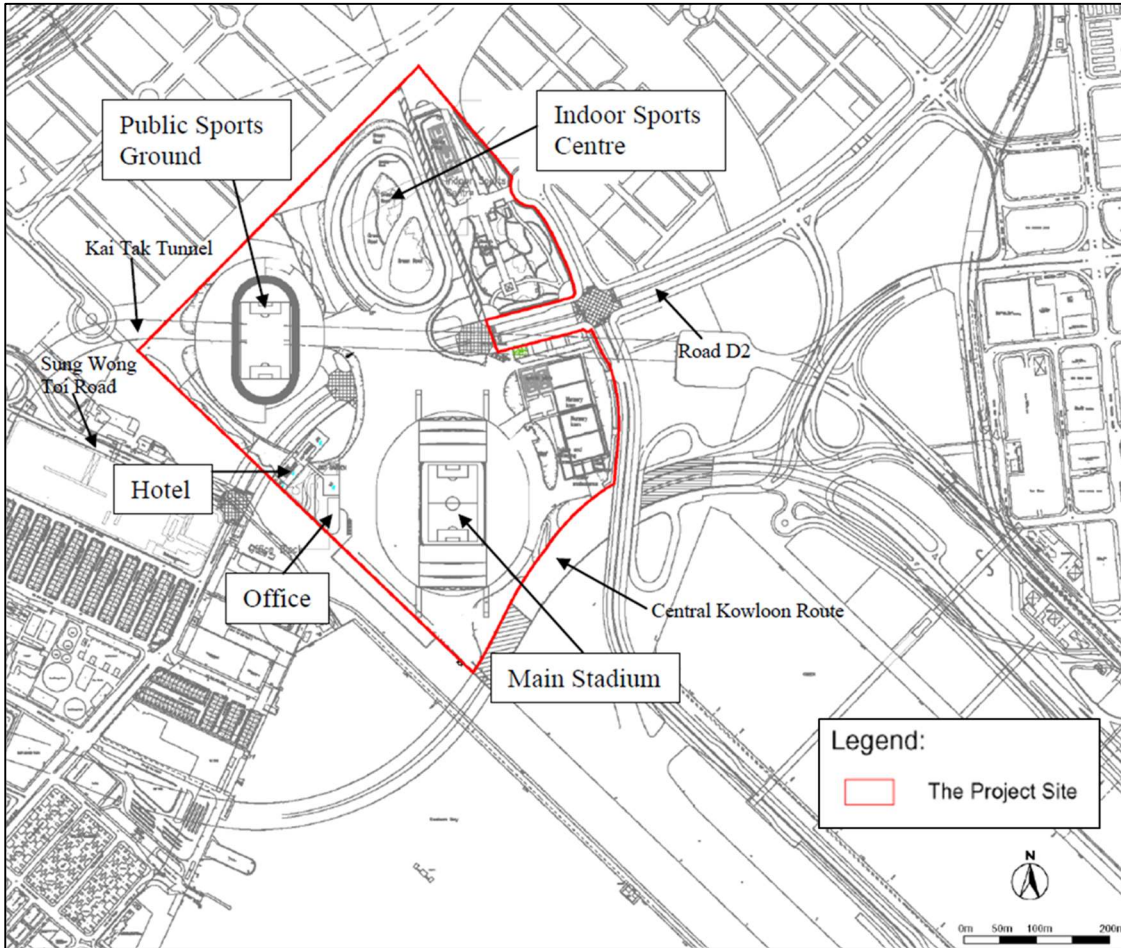

## Appendix C. Construction Programme



## Appendix D. Event and Action Plan

Should non-compliance of the air quality criteria occur, actions in accordance with the Event and Action Plan in **Table D.1** and **Table D.2** shall be carried out.

**Table D.1: Event and Action Plan for Construction Air Quality (Action Level)**

Event	Action			
	ET	IEC	SOR	Contracted Party
<b>Action Level</b>				
Exceedance for one sample	<ol style="list-style-type: none"> <li>1. Inform IEC, SOR and Contracted Party;</li> <li>2. Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>3. Repeat measurement to confirm finding.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contracted Party's working method.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify Contracted Party.</li> </ol>	<ol style="list-style-type: none"> <li>1. Rectify any unacceptable practice;</li> <li>2. Amend working methods if appropriate.</li> </ol>
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>1. Inform IEC, SOR and Contracted Party;</li> <li>2. Identify source;</li> <li>3. Advise the SOR on the effectiveness of the proposed remedial measures;</li> <li>4. Repeat measurements to confirm findings;</li> <li>5. Increase monitoring frequency to daily;</li> <li>6. Discuss with IEC, SOR and Contracted Party on remedial actions required;</li> <li>7. If exceedance continues, arrange meeting with IEC and SOR;</li> <li>8. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring data submitted by ET;</li> <li>2. Check Contracted Party's working method;</li> <li>3. Discuss with ET and Contracted Party on possible remedial measures;</li> <li>4. Advise the ET/SOR on the effectiveness of the proposed remedial measures;</li> <li>5. Supervise Implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contracted Party;</li> <li>3. Ensure remedial measures properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1. Submit proposals for remedial to SOR and IEC within 3 working days of notification;</li> <li>2. Implement the agreed proposals;</li> <li>3. Amend proposal if appropriate.</li> </ol>

**Table D.2: Event and Action Plan for Construction Air Quality (Limit Level)**

Event	Action			
	ET	IEC	SOR	Contracted Party
<b>Limit Level</b>				
Exceedance for one sample	1. Inform IEC, SOR, Contracted Party and EPD; 2. Identify source, investigate the causes of exceedance and propose remedial measures; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contracted Party's remedial actions and keep IEC, EPD and SOR informed of the results.	1. Check monitoring data submitted by ET; 2. Check Contracted Party's working method; 3. Discuss with ET and Contracted Party on possible remedial measures; 4. Advise the SOR on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. Ensure remedial measures properly implemented.	1. Take immediate action to avoid further exceedance; 2. Discuss with ET and IEC on remedial actions; 3. Submit proposals for remedial actions to IEC within 3 working days of notification; 4. Implement the agreed proposals; 5. Amend proposal if appropriate.
Exceedance for two or more consecutive samples	1. Notify IEC, SOR, Contracted Party and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contracted Party's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and SOR and Contracted Party to discuss the remedial actions to be taken; 7. Assess effectiveness of Contracted Party's remedial actions and keep IEC, EPD and SOR informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contracted Party's working method; 3. Discuss amongst SOR, ET, and Contracted Party on the potential remedial actions; 4. Review Contracted Party's remedial actions whenever necessary to assure their effectiveness and advise the SOR accordingly; 5. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. In consultation with the IEC, agree with the Contracted Party on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contracted Party to terminate that portion of work until the exceedance ceases.	1. Take immediate action to avoid further exceedance; 2. Discuss with ET and IEC on remedial actions; 3. Submit proposals for remedial actions to SOR and IEC within 3 working days of notification; 4. Implement the agreed proposals; 5. Resubmit proposals if problem still not under control; 6. Stop the relevant portion of works as determined by the SOR until the exceedance ceases.

Should non-compliance of the noise criteria occur, actions in accordance with the Event and Action Plan in **Table D.3** shall be carried out.

**Table D.3: Event and Action Plan for Construction Noise**

Event	Action			
	ET	IEC	SOR	Contracted Party
<b>Action Level</b>	1. Notify IEC, SOR and Contracted Party of exceedance; 2. Identify source; 3. Investigate the causes of exceedance and propose remedial measures; 4. Report the results of investigation to the IEC, SOR and Contracted Party; 5. Discuss with the IEC, SOR and Contracted Party and formulate remedial measures; 6. Increase monitoring frequency to check mitigation effectiveness.	1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contracted Party and advise the SOR accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. Require Contracted Party to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented	1. Submit noise mitigation proposals to SOR with copy to ET and IEC; 2. Implement noise mitigation proposals.
<b>Limit Level</b>	1. Inform IEC, SOR, EPD and Contracted Party; 2. Identify source; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contracted Party's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, SOR and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contracted Party's remedial actions and keep IEC, EPD and SOR informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst SOR, ET, and Contracted Party on the potential remedial actions; 2. Review Contracted Party's remedial actions whenever necessary to assure their effectiveness and advise the SOR accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contracted Party; 3. Require Contracted Party to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented; 5. If exceedance continues, investigate what portion of the work is responsible and instruct the Contracted Party to terminate that portion of work until the exceedance ceases.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to SOR with copy to ET and IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Terminate the relevant portion of works as determined by the SOR until the exceedance ceases.



# Appendix E. Environmental Site Inspection and Monitoring Schedule

**Table E.1: Site Inspection and Monitoring Schedule for November 2021**

Impact Environmental Monitoring Schedule for November 2021

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2	3 site inspection landscape and visual audit AMS1, NMS1 AMS2, NMS2	4	5	6
7	8	9 AMS1, NMS1 AMS2, NMS2	10 site inspection	11	12	13
14	15 AMS1, NMS1 AMS2, NMS2	16	17 site inspection landscape and visual audit	18	19 AMS1 AMS2	20
21	22	23 site inspection	24	25 AMS1, NMS1 AMS2, NMS2	26	27
28	29	30				

 Air Quality/Noise Monitoring

Remark: Joint site walk with IEC on 10 and 23 November 2021

**Table E.2: Tentative Site Inspection and Monitoring Schedule for December 2021**

Tentative Impact Environmental Monitoring Schedule for December 2021

Sun	Mon	Tue	Wed	Thu	Fri	Sat
			1 site inspection AMS1, NMS1 AMS2, NMS2	2	3	4
5	6	7 AMS1, NMS1 AMS2, NMS2	8 site inspection landscape and visual audit	9	10	11
12	13 AMS1, NMS1 AMS2, NMS2	14	15 site inspection	16	17 AMS1 AMS2	18
19	20	21	22 site inspection landscape and visual audit	23 AMS1, NMS1 AMS2, NMS2	24	25 Christmas Day
26	27 The first weekday after Christmas Day	28	29 site inspection AMS1, NMS1 AMS2, NMS2	30	31	

 Air Quality/Noise Monitoring

Remark: The schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather, etc)

## Appendix F. Calibration Certificates



## ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

### SUB-CONTRACTING REPORT

CONTACT	: MR K.W. FAN	WORK ORDER	: <b>HK2117311</b>
CLIENT	: ENVIROTECH SERVICES CO.		
ADDRESS	: RM113, 1/F, MY LOFT, 9 HOI WING ROAD, TUEN MUN, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 29-APR-2021
		DATE OF ISSUE	: 11-MAY-2021
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

#### General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd  
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong  
Tel. +852 2610 1044 Fax: +852 2610 2021 www.alsglobal.com

WORK ORDER : HK2117311  
SUB-BATCH : 1  
CLIENT : ENVIROTECH SERVICES CO.  
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2117311-001	S/N: 226239	Equipments	29-Apr-2021	S/N: 226239

## Equipment Verification Report (TSP)

### Equipment Calibrated:

Type: Laser Dust monitor  
Manufacturer: Sibata LD-3B  
Serial No. 2Z6239  
Equipment Ref: Nil  
Job Order HK2117311

### Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)  
Location & Location ID: AUES office (calibration room)  
Equipment Ref: HVS 018  
Last Calibration Date: 26 April 2021


### Equipment Verification Results:

Verification Date: 7 May 2021

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m <sup>3</sup> (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr	09:30 ~ 11:30	26.6	1013.2	0.046	3830	31.9
2hr01min	11:32 ~ 13:33	26.6	1013.2	0.035	3245	26.9
2hr10min	13:35 ~ 15:45	26.6	1013.2	0.036	3369	26.0

### Linear Regression of Y or X

Slope (K-factor): 0.0014  
Correlation Coefficient 0.9954  
Date of Issue 10 May 2021

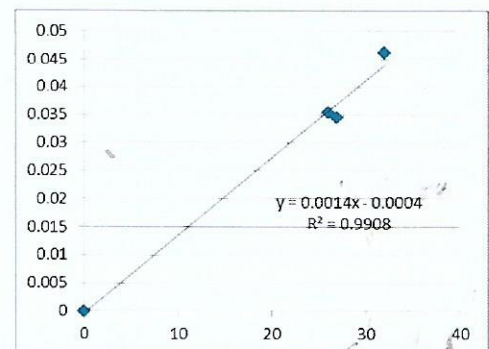

### Remarks:

1. **Strong Correlation (R>0.8)**
2. Factor 0.0014 should be applied for TSP monitoring

\*If R<0.5, repair or re-verification is required for the equipment

Operator : Fai So Signature :  Date : 10 May 2021

QC Reviewer : Ben Tam Signature :  Date : 10 May 2021



## ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES

### SUB-CONTRACTING REPORT

CONTACT : MR K.W. FAN	WORK ORDER : <b>HK2117310</b>
CLIENT : ENVIROTECH SERVICES CO.	
ADDRESS : RM113, 1/F, MY LOFT, 9 HOI WING ROAD, TUEN MUN, N.T. HONG KONG	SUB-BATCH : 1
	DATE RECEIVED : 29-APR-2021
	DATE OF ISSUE : 11-MAY-2021
PROJECT : ---	NO. OF SAMPLES : 1
	CLIENT ORDER : ---

#### General Comments

- Sample(s) was/ were submitted by client. Sample(s) arrived laboratory in ambient condition. The result(s) related only to the item(s) tested.
- Sample information (Project name, Sample ID, Sampling date/time, etc.) is provided by client.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

#### Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

Managing Director

This is the Final Report and supersedes any preliminary report with this batch number.

All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd  
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong  
Tel. +852 2610 1044 Fax: +852 2610 2021 www.alsglobal.com

WORK ORDER : HK2117310  
SUB-BATCH : 1  
CLIENT : ENVIROTECH SERVICES CO.  
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK2117310-001	S/N: 276017	Equipments	29-Apr-2021	S/N: 276017



## Equipment Verification Report (TSP)

### Equipment Calibrated:

Type: Laser Dust monitor  
Manufacturer: Sibata LD-3B  
Serial No. 276017  
Equipment Ref: Nil  
Job Order HK2117310

### Standard Equipment:

Standard Equipment: Higher Volume Sampler (TSP)  
Location & Location ID: AUES office (calibration room)  
Equipment Ref: HVS 018  
Last Calibration Date: 26 April 2021


### Equipment Verification Results:

Verification Date: 7 May 2021

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m <sup>3</sup> (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/min)
2hr	09:30 ~ 11:30	26.6	1013.2	0.046	3951	32.9
2hr01min	11:32 ~ 13:33	26.6	1013.2	0.035	3293	27.3
2hr10min	13:35 ~ 15:45	26.6	1013.2	0.036	3519	27.2

### Linear Regression of Y or X

Slope (K-factor): 0.0014  
Correlation Coefficient 0.9963  
Date of Issue 10 May 2021

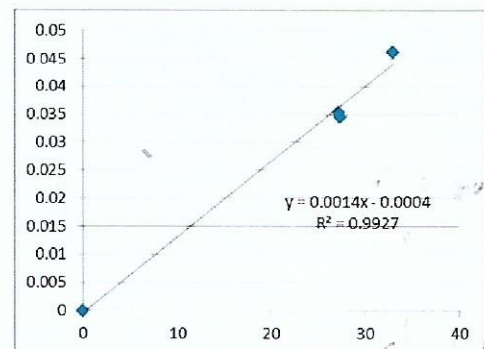

### Remarks:

1. **Strong Correlation (R>0.8)**
  2. Factor 0.0014 should be applied for TSP monitoring
- \*if R<0.5, repair or re-verification is required for the equipment

Operator : Fai So Signature : *Fai So* Date : 10 May 2021

QC Reviewer : Ben Tam Signature : *Ben Tam* Date : 10 May 2021



# Certificate of Calibration 校正證書

Certificate No. : C210001  
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC20-2688) Date of Receipt / 收件日期 : 18 December 2020

Description / 儀器名稱 : Precision Acoustic Calibrator  
Manufacturer / 製造商 : LARSON DAVIS  
Model No. / 型號 : CAL200  
Serial No. / 編號 : 11334  
Supplied By / 委託者 : Envirotech Services Co.  
Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,  
New Territories, Hong Kong

## TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$  Relative Humidity / 相對濕度 :  $(50 \pm 25)\%$   
Line Voltage / 電壓 : ---

## TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 2 January 2021

## TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.  
The results do not exceed manufacturer's specification & user's specified acceptance criteria.  
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA

Tested By :   
測試 : H T Wong  
Assistant Engineer

Certified By :   
核證 : K C Lee  
Engineer

Date of Issue : 4 January 2021  
簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C210001  
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C203952
CL281	Multifunction Acoustic Calibrator	CDK1806821
TST150A	Measuring Amplifier	C201309

- Test procedure : MA100N.

- Results :

### 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	User's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	93.7	± 0.5	± 0.2
114 dB, 1 kHz	113.7		

### 5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000	1 kHz ± 1 %	± 1


Remarks : - The user's specified acceptance criteria (user's spec.) is a customer pre-defined operating tolerance of the UUT, suitable for one's own intended use.

- The uncertainties are for a confidence probability of not less than 95 %.

### Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

# Certificate of Calibration

## 校正證書

Certificate No. : C213255

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC21-1016)

Date of Receipt / 收件日期 : 24 May 2021

Description / 儀器名稱 : Sound Level Meter

Manufacturer / 製造商 : Rion

Model No. / 型號 : NL-52

Serial No. / 編號 : 00131627

Supplied By / 委託者 : Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,  
New Territories, Hong Kong

### TEST CONDITIONS / 測試條件

Temperature / 溫度 :  $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 :  $(50 \pm 25)\%$

Line Voltage / 電壓 : ---

### TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 4 June 2021

### TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.


The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA


Tested By

測試

  
K P Cheuk  
Project Engineer

Certified By

核證

  
K C Lee  
Engineer

Date of Issue

簽發日期

9 June 2021

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

# Certificate of Calibration

## 校正證書

Certificate No. : C213255  
證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C210084
CL281	Multifunction Acoustic Calibrator	AV210017

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	94.2	± 1.1

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	94.2 (Ref.)
				104.00		104.2
				114.00		114.2

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

- 6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L <sub>A</sub>	A	Fast	94.00	1	94.2	Ref.
			Slow				

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

# Certificate of Calibration

## 校正證書

Certificate No. : C213255

證書編號

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L <sub>A</sub>	A	Fast	94.00	63 Hz	68.0	-26.2 ± 1.5
					125 Hz	78.0	-16.1 ± 1.5
					250 Hz	85.5	-8.6 ± 1.4
					500 Hz	91.0	-3.2 ± 1.4
					1 kHz	94.2	Ref.
					2 kHz	95.4	+1.2 ± 1.6
					4 kHz	95.2	+1.0 ± 1.6
					8 kHz	93.2	-1.1 (+2.1 ; -3.1)
					16 kHz	86.2	-6.6 (+3.5 ; -17.0)

#### 6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L <sub>C</sub>	C	Fast	94.00	63 Hz	93.3	-0.8 ± 1.5
					125 Hz	94.0	-0.2 ± 1.5
					250 Hz	94.2	0.0 ± 1.4
					500 Hz	94.2	0.0 ± 1.4
					1 kHz	94.2	Ref.
					2 kHz	94.0	-0.2 ± 1.6
					4 kHz	93.4	-0.8 ± 1.6
					8 kHz	91.3	-3.0 (+2.1 ; -3.1)
					16 kHz	84.3	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

# Certificate of Calibration

## 校正證書

Certificate No. : C213255  
證書編號

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 10446

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB	: 63 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	16 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com


## **Appendix G. Monitoring Data and Graphical Plots (Air Quality and Noise)**



## Data for 1-hour TSP Monitoring at Station AMS1 during the Reporting Month

Date	Start Time	Finish Time	Weather	Wind Speed (m/s)	Wind Direction (deg)	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )
3-Nov-21	9:08	10:08	Fine	4.7	93	32
3-Nov-21	10:08	11:08	Fine	3.3	109	28
3-Nov-21	11:08	12:08	Fine	4.7	84	35
9-Nov-21	9:07	10:07	Cloudy	1.4	325	34
9-Nov-21	10:07	11:07	Cloudy	1.4	242	37
9-Nov-21	11:07	12:07	Cloudy	1.1	192	32
15-Nov-21	9:15	10:15	Sunny	4.4	96	27
15-Nov-21	10:15	11:15	Sunny	3.9	105	31
15-Nov-21	11:15	12:15	Sunny	2.2	94	24
19-Nov-21	9:06	10:06	Cloudy	3.1	85	39
19-Nov-21	10:06	11:06	Cloudy	3.3	95	44
19-Nov-21	11:06	12:06	Cloudy	2.8	108	46
25-Nov-21	10:00	11:00	Fine	1.4	287	45
25-Nov-21	11:00	12:00	Fine	1.1	214	44
25-Nov-21	12:00	13:00	Fine	1.7	215	46


## Graphical Presentation for 1-hour TSP Monitoring at AMS1

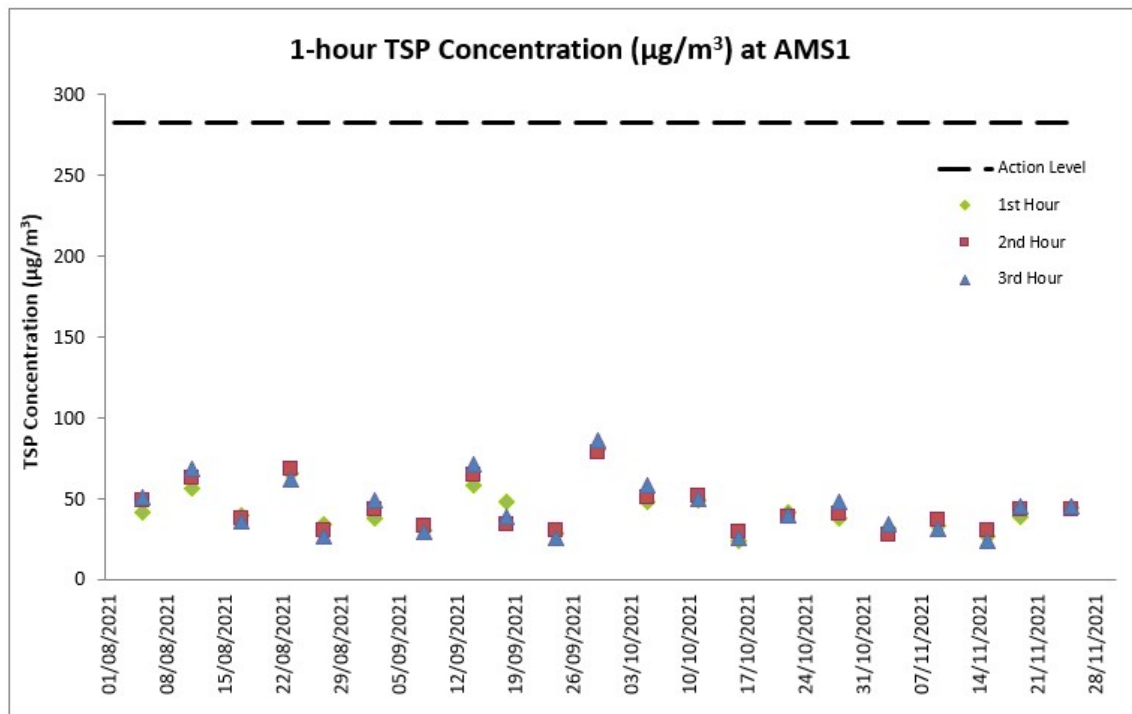

## Data for 1-hour TSP Monitoring at Station AMS2 during the Reporting Month

Date	Start Time	Finish Time	Weather	Wind Speed (m/s)	Wind Direction (deg)	1-hour TSP ( $\mu\text{g}/\text{m}^3$ )
3-Nov-21	8:23	9:23	Fine	5.3	100	36
3-Nov-21	9:23	10:23	Fine	5.3	101	40
3-Nov-21	10:23	11:23	Fine	5.3	108	33
9-Nov-21	9:07	10:07	Cloudy	1.4	325	44
9-Nov-21	10:07	11:07	Cloudy	1.4	242	49
9-Nov-21	11:07	12:07	Cloudy	1.1	192	51
15-Nov-21	8:27	9:27	Sunny	2.2	2	36
15-Nov-21	9:27	10:27	Sunny	4.7	102	40
15-Nov-21	10:27	11:27	Sunny	3.3	37	35
19-Nov-21	8:40	9:40	Sunny	3.1	97	50
19-Nov-21	9:40	10:40	Sunny	3.3	106	45
19-Nov-21	10:40	11:40	Sunny	3.1	81	42
25-Nov-21	9:04	10:04	Fine	1.1	246	50
25-Nov-21	10:04	11:04	Fine	0.8	variable	39
25-Nov-21	11:04	12:04	Fine	1.1	220	35


## Graphical Presentation for 1-hour TSP Monitoring at AMS2

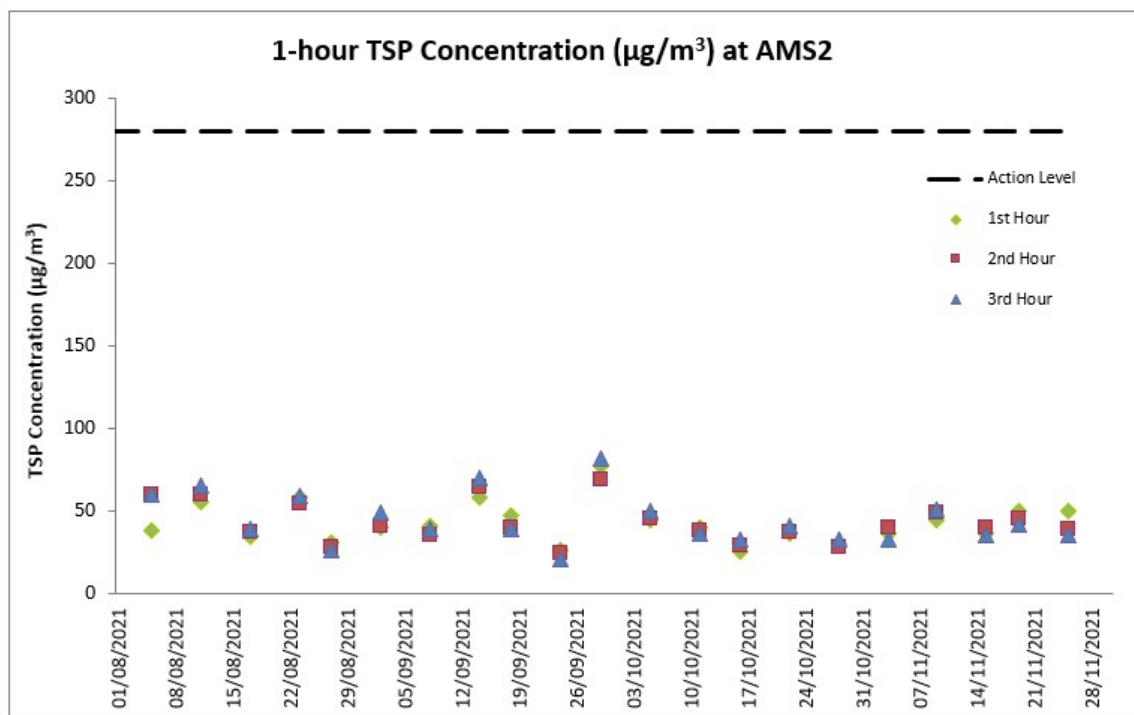

### Data for Noise Monitoring at Station NMS1 during the Reporting Month

Date	Time	Weather	L <sub>eq(5min)</sub>	L <sub>10</sub>	L <sub>90</sub>	Measured L <sub>eq(30min)</sub>
3-Nov-21	9:10	Fine	69.9	71.0	67.7	68.6
3-Nov-21	9:15	Fine	68.1	70.2	66.4	
3-Nov-21	9:20	Fine	68.3	70.5	66.8	
3-Nov-21	9:25	Fine	67.2	69.4	65.7	
3-Nov-21	9:30	Fine	69.5	71.6	67.4	
3-Nov-21	9:35	Fine	68.2	70.7	66.6	
9-Nov-21	9:09	Cloudy	68.2	70.8	66.0	68.6
9-Nov-21	9:14	Cloudy	69.1	71.7	67.5	
9-Nov-21	9:19	Cloudy	69.1	71.2	67.7	
9-Nov-21	9:24	Cloudy	68.3	70.6	66.4	
9-Nov-21	9:29	Cloudy	68.2	70.5	66.9	
9-Nov-21	9:34	Cloudy	68.6	71.4	67.6	
15-Nov-21	9:07	Sunny	67.9	69.0	65.7	68.4
15-Nov-21	9:12	Sunny	68.1	70.6	66.2	
15-Nov-21	9:17	Sunny	68.1	70.3	66.8	
15-Nov-21	9:22	Sunny	67.4	69.2	65.5	
15-Nov-21	9:27	Sunny	68.7	70.6	66.5	
15-Nov-21	9:32	Sunny	69.6	71.7	67.8	
25-Nov-21	9:57	Fine	68.2	71.3	63.2	68.3
25-Nov-21	10:02	Fine	69.4	72.5	64.5	
25-Nov-21	10:07	Fine	68.8	71.4	64.9	
25-Nov-21	10:12	Fine	68.8	72.1	64.7	
25-Nov-21	10:17	Fine	66.8	69.8	64.9	
25-Nov-21	10:22	Fine	67.5	70.3	64.6	


### Graphical Presentation for Noise Monitoring at NMS1

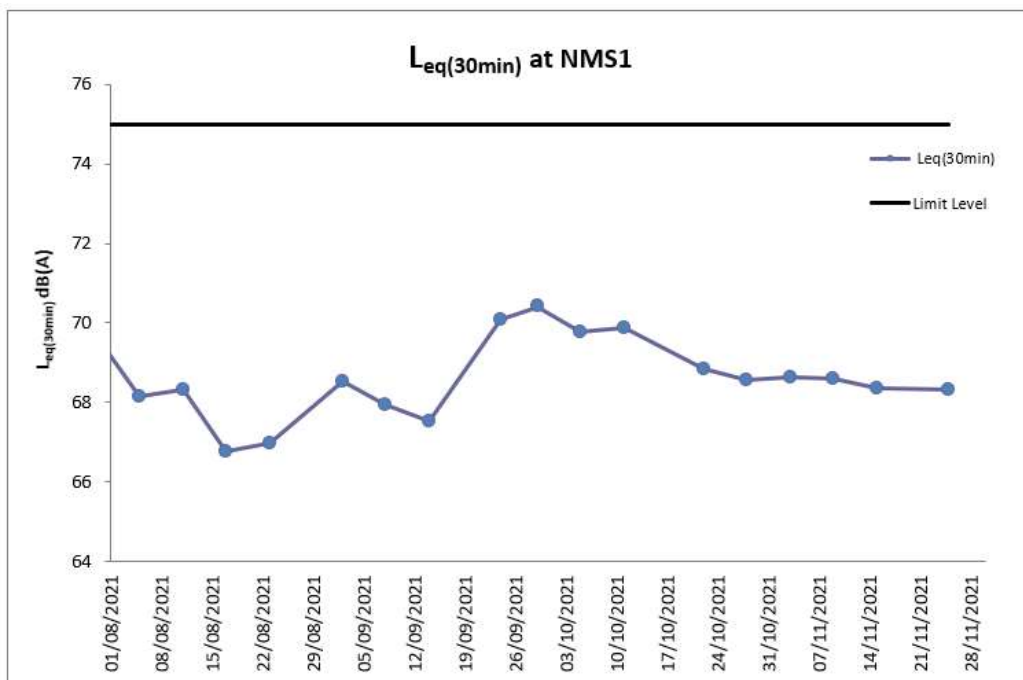

### Data for Noise Monitoring at Station NMS2 during the Reporting Month



Date	Time	Weather	L <sub>eq</sub> (5min)	L <sub>10</sub>	L <sub>90</sub>	Measured L <sub>eq</sub> (30min)
3-Nov-21	8:25	Fine	67.0	69.3	65.5	
3-Nov-21	8:30	Fine	68.4	70.1	66.6	
3-Nov-21	8:35	Fine	67.2	69.2	65.7	68.2
3-Nov-21	8:40	Fine	69.1	71.3	67.6	
3-Nov-21	8:45	Fine	68.4	70.5	66.8	
3-Nov-21	8:50	Fine	68.7	70.6	66.9	
9-Nov-21	8:22	Cloudy	68.6	70.4	65.2	
9-Nov-21	8:27	Cloudy	67.5	69.2	64.3	
9-Nov-21	8:32	Cloudy	67.1	69.6	64.8	67.6
9-Nov-21	8:37	Cloudy	66.7	68.1	65.5	
9-Nov-21	8:42	Cloudy	68.0	70.2	66.1	
9-Nov-21	8:47	Cloudy	67.6	68.8	64.9	
15-Nov-21	8:30	Sunny	67.2	69.0	65.4	
15-Nov-21	8:35	Sunny	67.1	69.2	65.3	
15-Nov-21	8:40	Sunny	66.1	68.3	64.4	67.3
15-Nov-21	8:45	Sunny	68.6	70.5	66.8	
15-Nov-21	8:50	Sunny	67.6	69.7	65.2	
15-Nov-21	8:55	Sunny	67.1	69.9	65.7	
25-Nov-21	9:07	Fine	72.7	76.8	66.5	
25-Nov-21	9:12	Fine	70.6	72.5	65.7	
25-Nov-21	9:17	Fine	70.8	73.4	65.2	71.2
25-Nov-21	9:22	Fine	70.3	72.6	66.4	
25-Nov-21	9:27	Fine	70.4	73.1	65.1	
25-Nov-21	9:32	Fine	72.0	74.0	65.6	

### Graphical Presentation for Noise Monitoring at NMS2


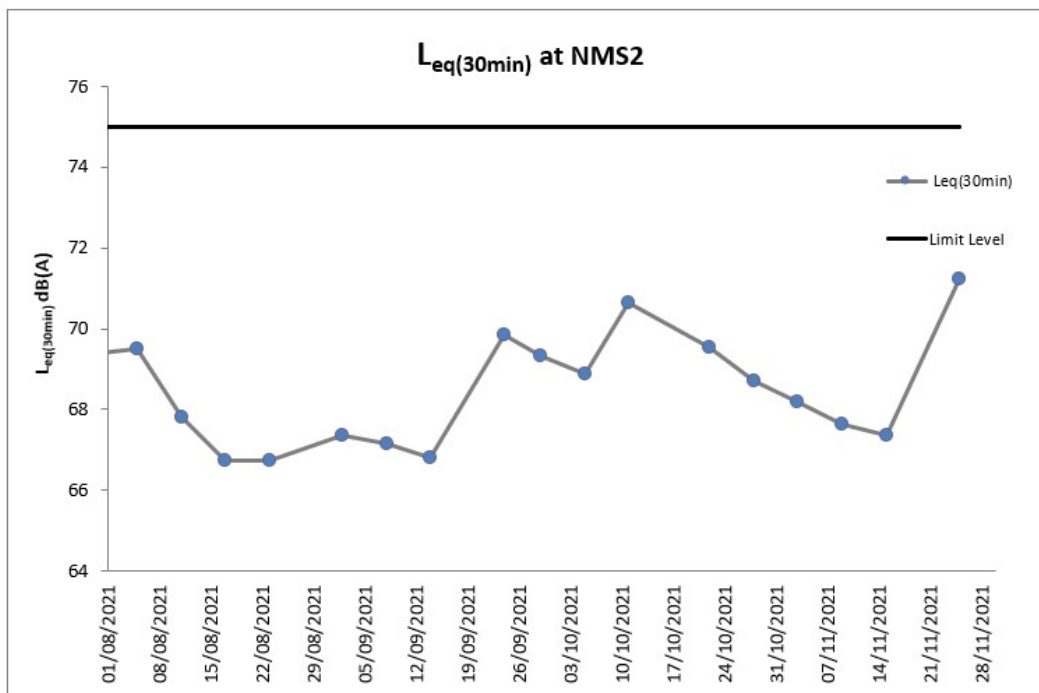


## Appendix H. Wind Data



3 November 2021

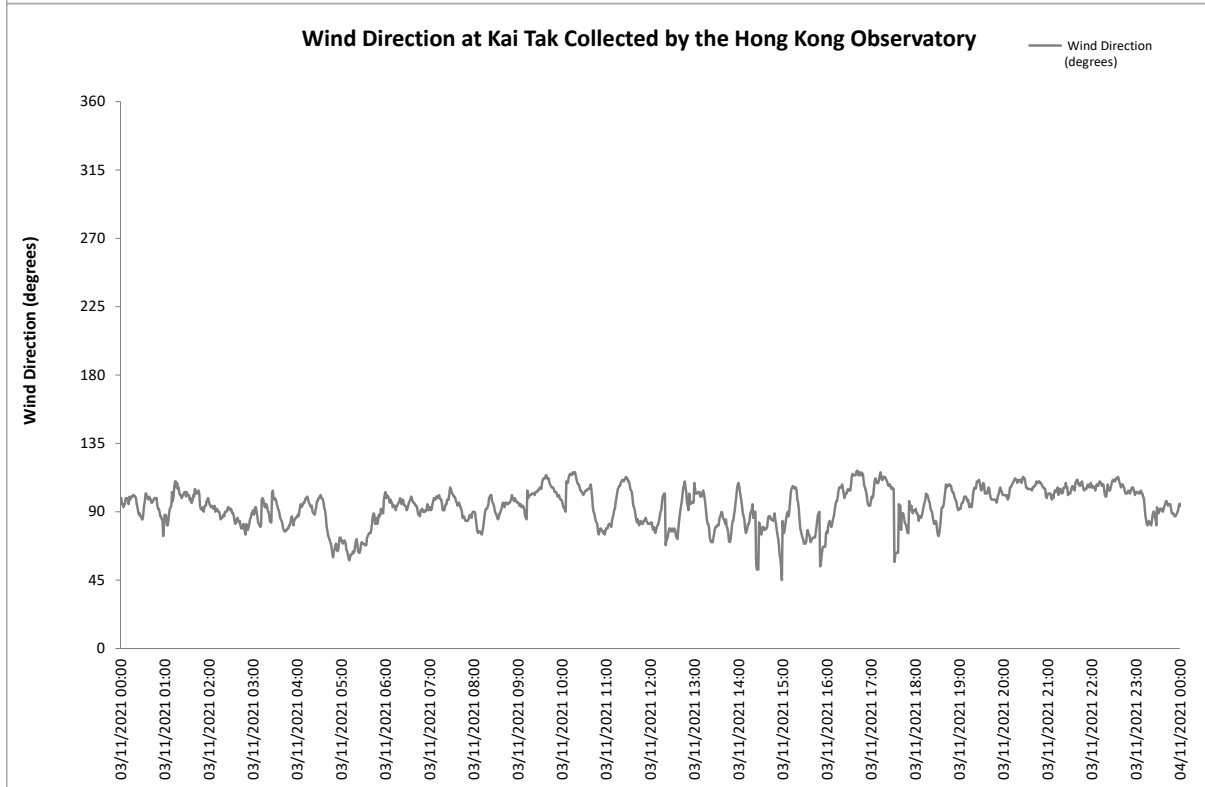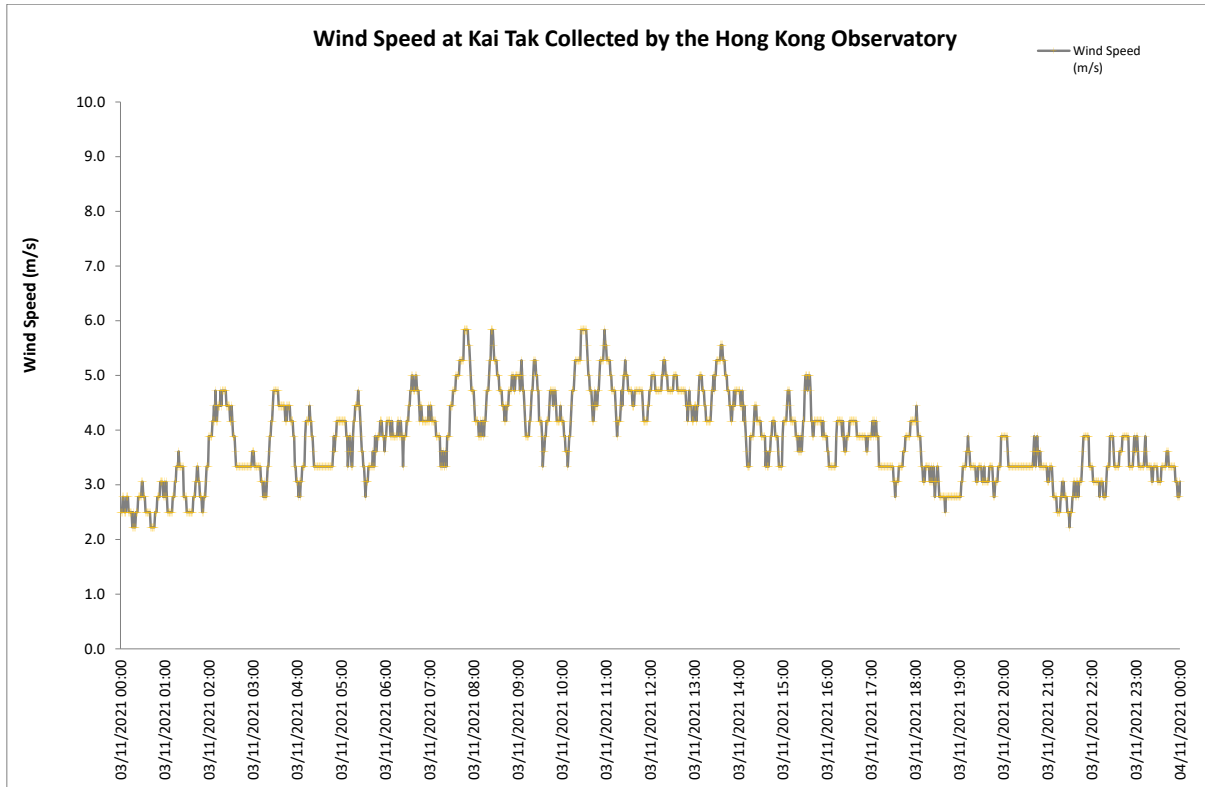

9 November 2021

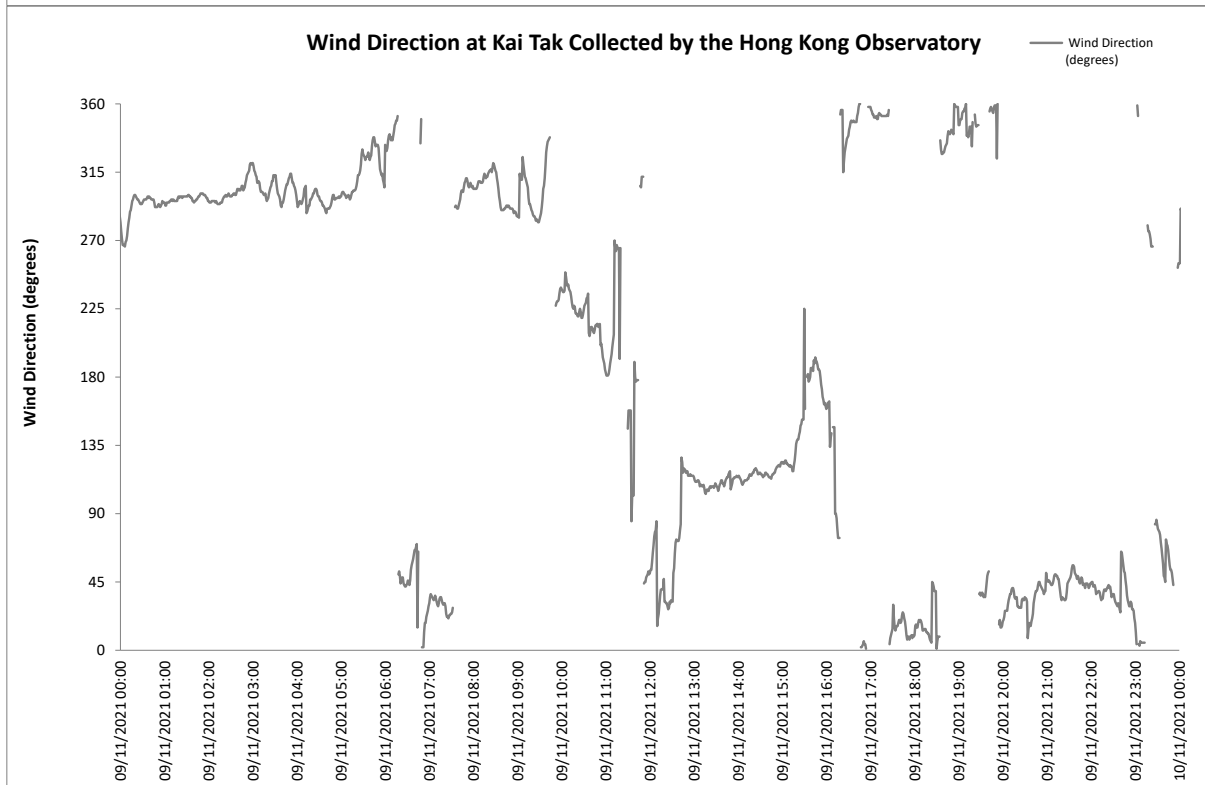
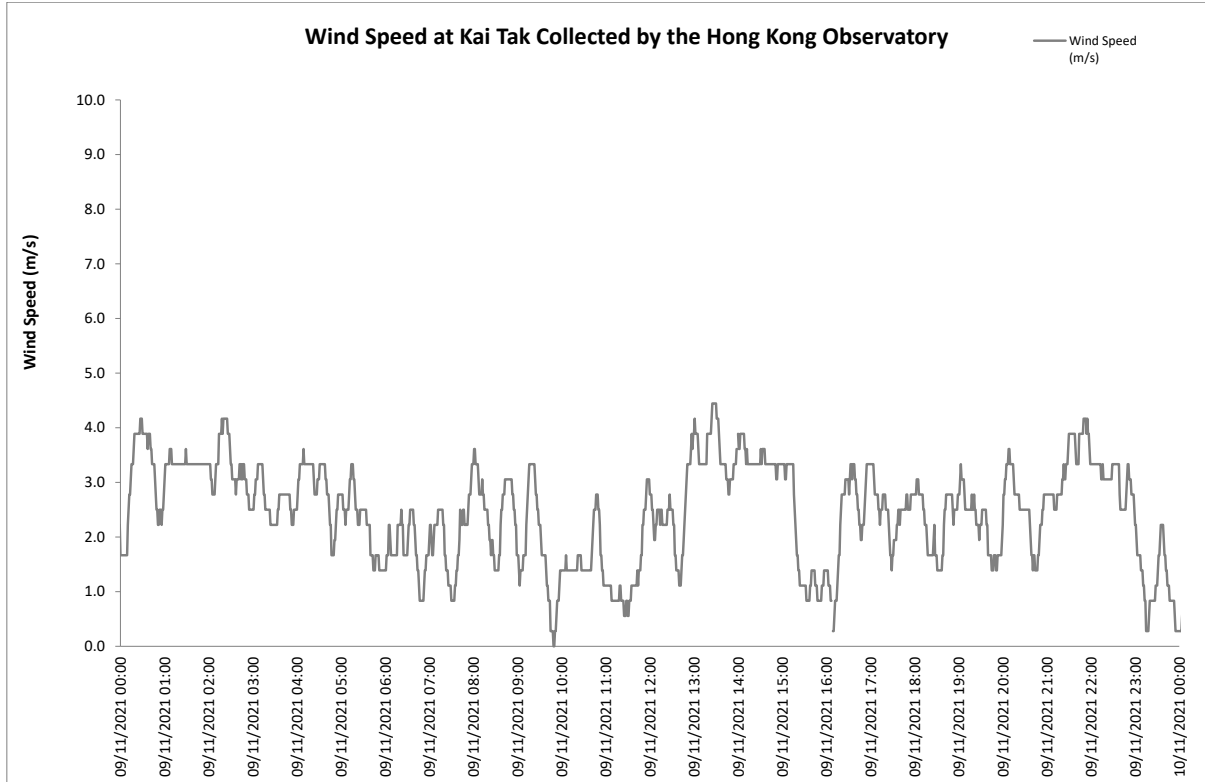


15 November 2021

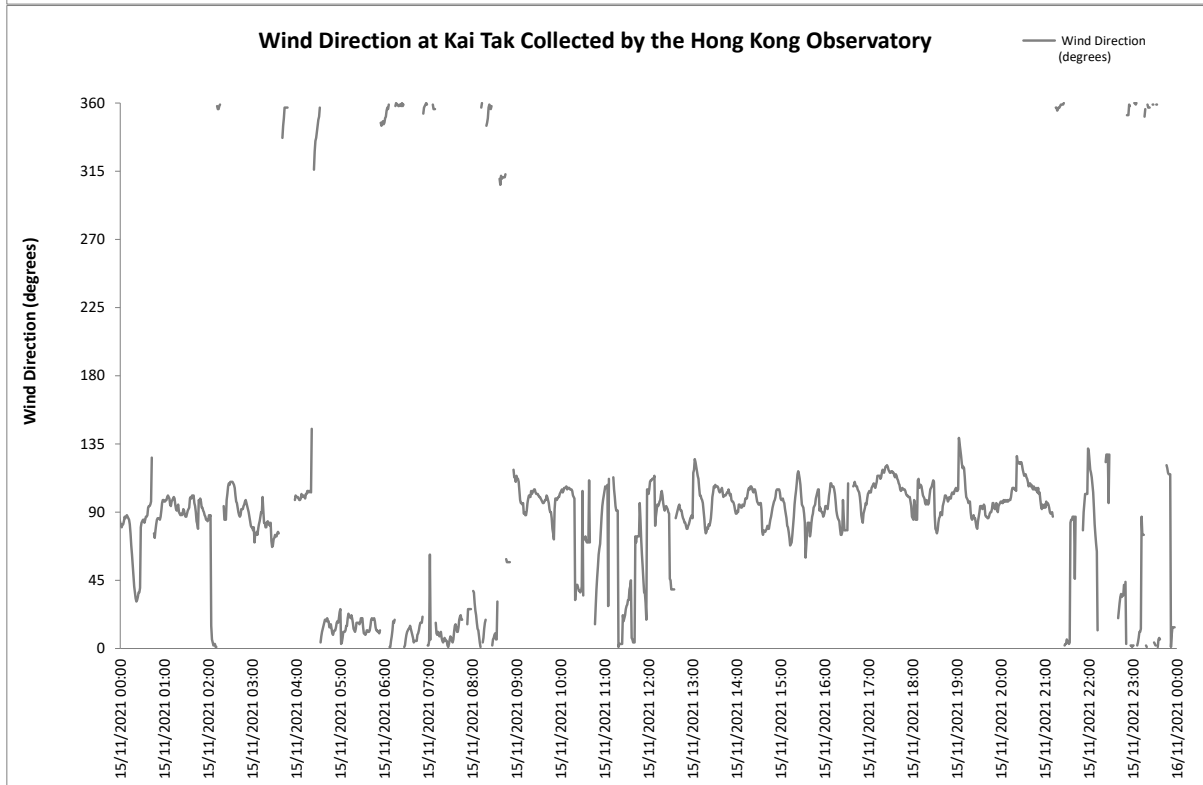
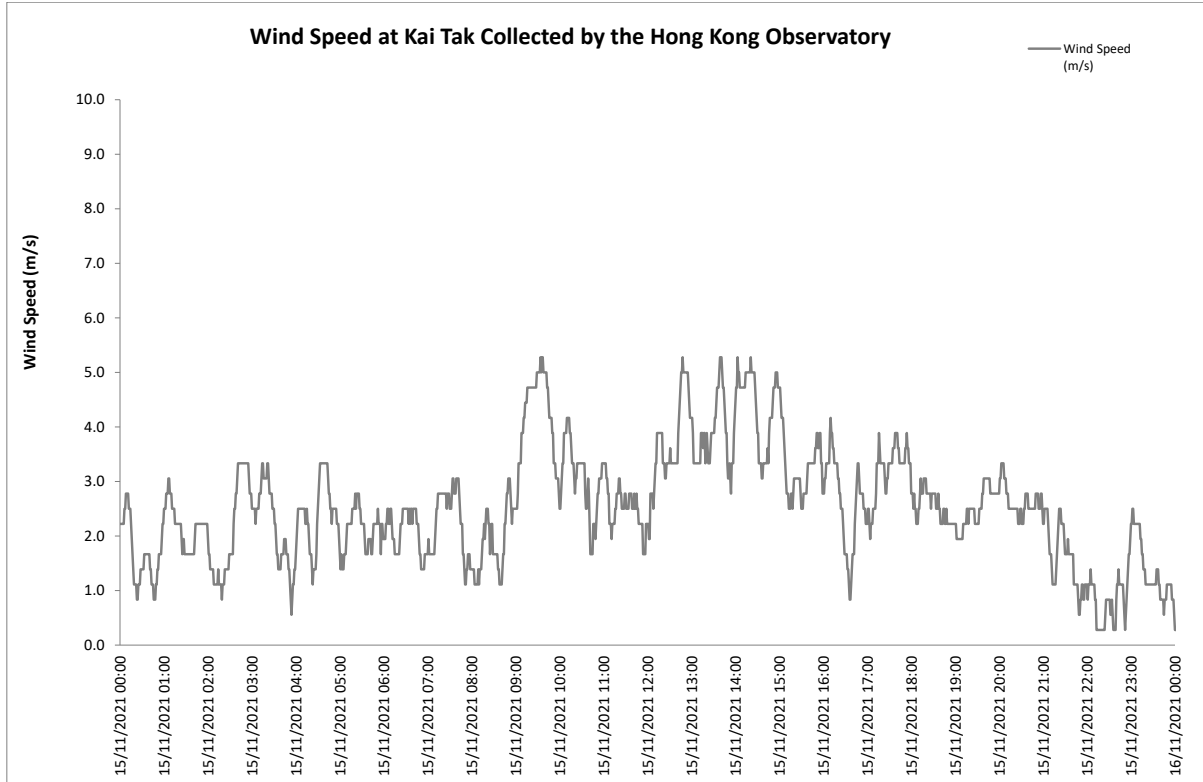




19 November 2021

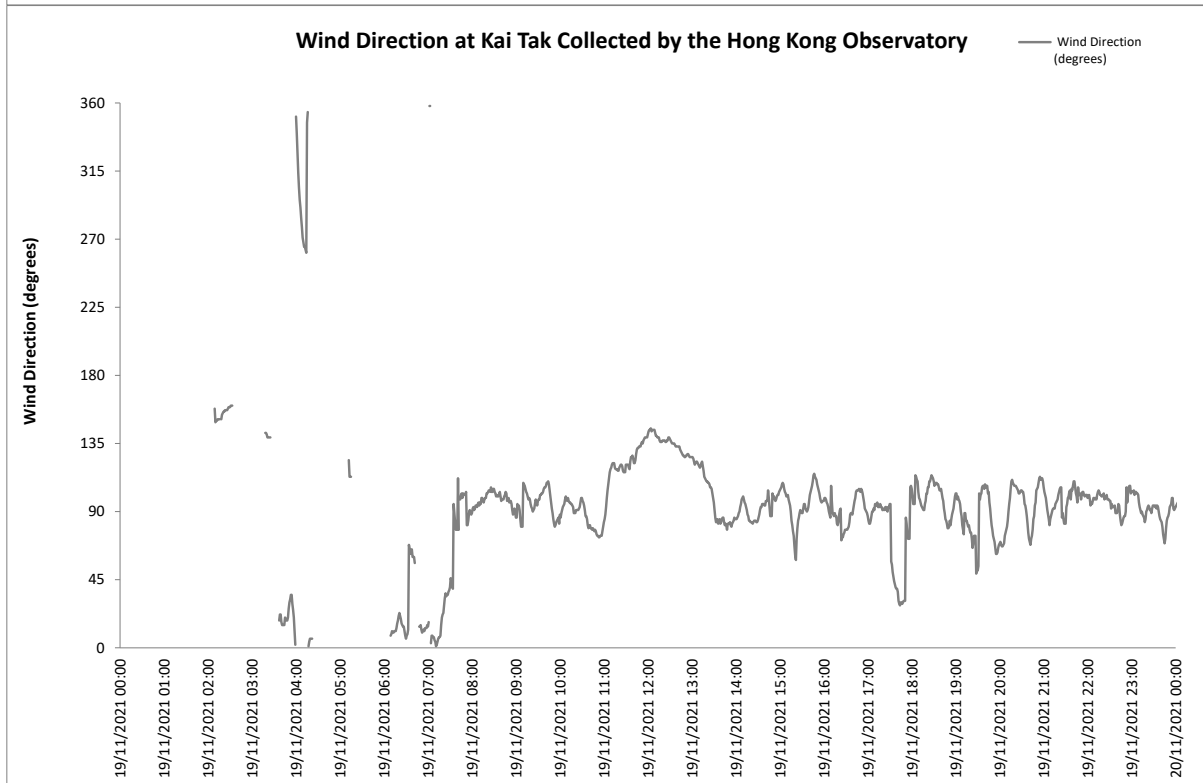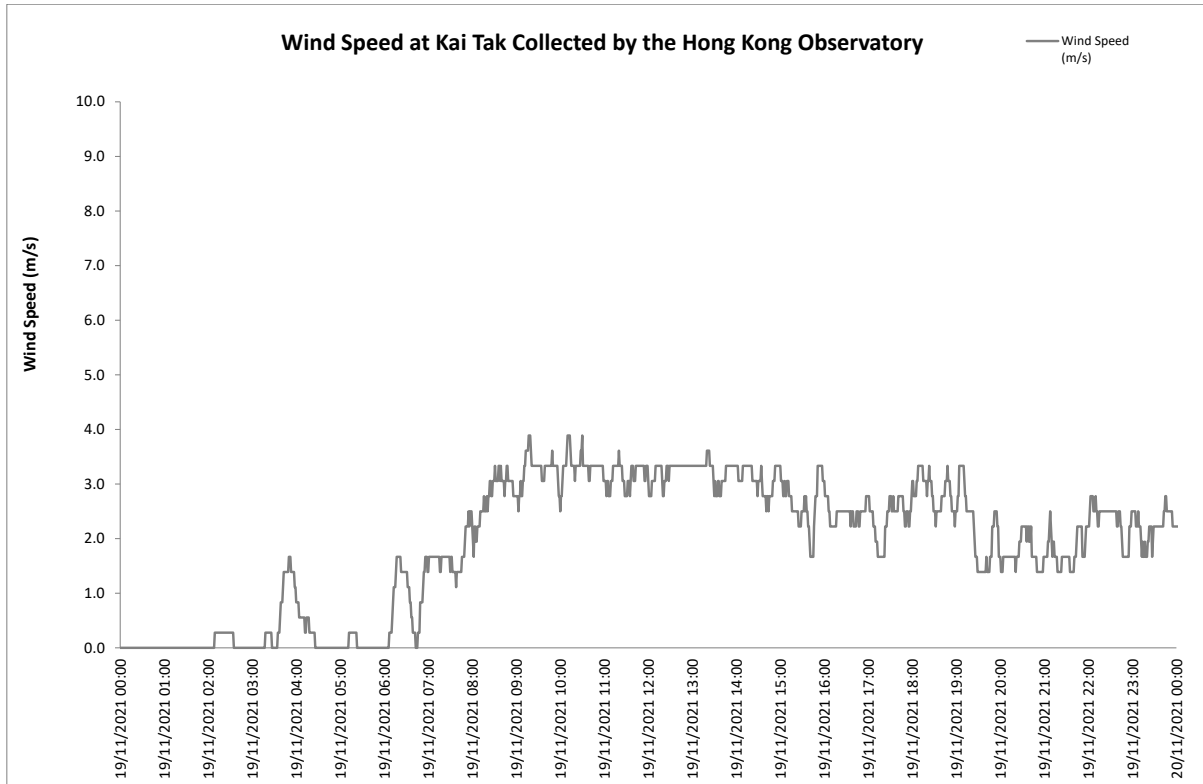

25 November 2021

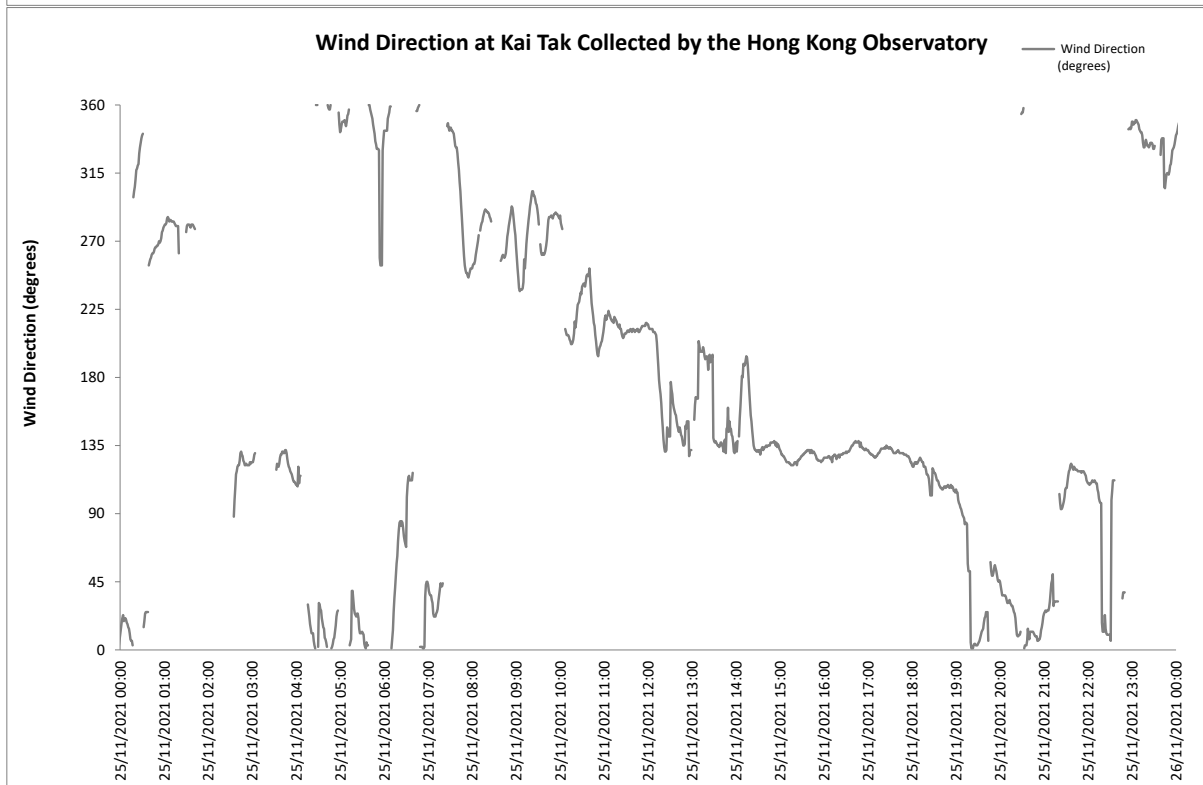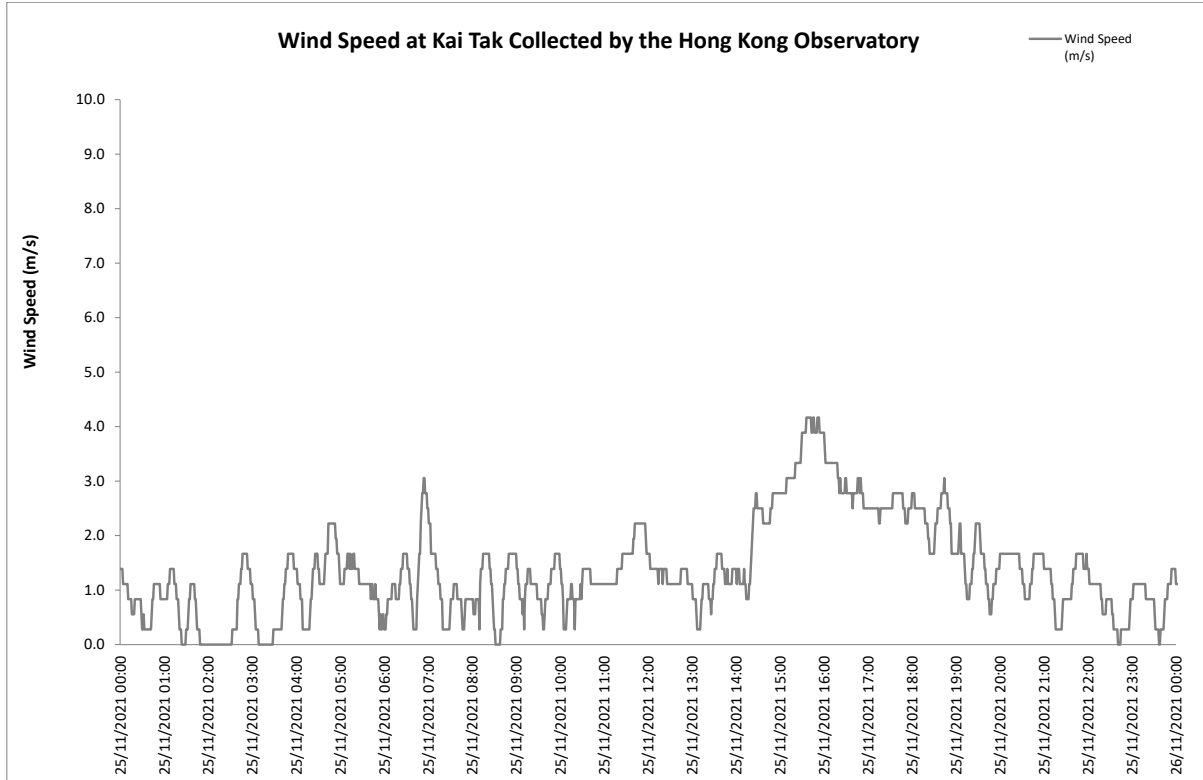

## Appendix I. Waste Flow Table

Project: Kai Tak Sport Park  
 Contract No.: HAB/ KTSP/ 01  
 Contract Title: Design, Construction and Operation of the Kai Tak Sports Park at Kai Tak, Kowloon City District, Hong Kong  
 Year of Record: 2019-2021



### Monthly Waste Flow Table

Month	Total Quantity Generated	Total Quantity Generated (Excluded Excavated Material)	Actual Quantities of Inert C&D Materials Generated Monthly								Actual Quantities of C&D Materials Generated Monthly						Remarks
			Excavated Materials			Non-excavated Materials					Metals (steel bar / metal strip) <sup>(1)</sup>	Metals (aluminum can) <sup>(1)</sup>	Paper / cardboard packaging <sup>(1)</sup>	Plastics <sup>(1) &amp; (4)</sup>	Chemical waste (wasted lubricant oil/ oil container)	Other, e.g. general refuse	
			Disposed in Public Fill	Disposed in Sorting Facilities	Others (e.g. Reused in the Contract / Other Projects)	Broken Concrete or Construction Waste Collected by Recycled Company	Reused in the Contract	Reused in other Projects	Disposed in Public Fill	Disposed in Sorting Facilities							
											(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	
a1	a2	b	b	b	c	d	e	f	g	h	i	j	k	l	m		
Jan-19																	
Feb-19	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
Mar-19	4960.89	4741.39	219.50	0.00	0.00	0.00	0.00	219.50	0.00	0.00	11.84	0.00	0.00	0.00	0.00	4729.55	
Apr-19	1218.47	1211.81	6.66	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.06	0.00	0.00	1211.75	
May-19	87.29	87.29	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.01	0.00	0.00	87.28	
Jun-19	80.77	80.77	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.67	0.00	0.08	0.42	0.00	79.61	
Jul-19	2302.16	614.79	1687.37	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.30	0.95	0.00	613.54	
Aug-19	3619.81	280.59	3339.22	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.77	0.00	0.00	1.29	0.60	276.93	
Sep-19	9840.16	349.65	9490.51	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.04	0.60	348.01	
Oct-19	11505.06	543.69	10961.37	0.00	0.00	0.00	0.00	0.00	0.00	0.00	81.95	0.00	1.43	1.15	0.00	459.16	
Nov-19	4718.13	313.84	4404.29	0.00	0.00	0.00	0.00	0.00	0.00	0.00	69.84	0.00	0.24	1.37	0.00	242.39	
Dec-19	5185.14	102.48	5082.66	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.63	0.80	100.05	
Jan-20	12107.08	127.05	11980.03	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.32	0.00	0.57	1.36	0.00	108.80	
Feb-20	18104.96	100.58	13459.32	0.00	4545.06	0.00	0.00	0.00	0.00	0.00	23.64	0.00	0.00	0.96	0.00	75.98	
Mar-20	35699.19	235.99	6615.03	0.00	28848.17	0.00	0.00	0.00	0.00	0.00	90.73	0.00	0.50	1.33	0.80	142.63	
Apr-20	42587.03	137.90	0.00	0.00	42449.13	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.10	0.00	136.80	
May-20	64506.51	218.89	0.00	0.00	64287.62	0.00	0.00	0.00	0.00	0.00	47.41	0.00	0.40	1.61	0.00	169.47	
Jun-20	44983.53	337.20	6519.25	0.00	38127.08	0.00	0.00	0.00	0.00	0.00	171.56	0.00	0.58	2.55	0.80	161.71	
Jul-20	43468.97	602.89	0.00	0.00	42866.08	0.00	0.00	0.00	0.00	0.00	377.41	0.01	1.03	2.16	0.00	222.28	
Aug-20	61609.05	1121.82	3771.32	0.00	56715.91	0.00	0.00	0.00	0.00	0.00	861.33	0.35	1.58	2.35	0.00	256.21	
Sep-20	111046.04	730.59	0.00	0.00	110315.45	0.00	0.00	0.00	0.00	0.00	443.46	0.01	1.39	1.87	0.00	283.86	
Oct-20	109678.75	712.61	0.00	0.00	108966.14	0.00	0.00	0.00	0.00	0.00	385.68	0.02	1.00	1.64	0.00	324.27	
Nov-20	135055.14	852.56	0.00	0.00	134202.58	0.00	0.00	0.00	0.00	0.00	362.36	0.01	0.86	2.12	0.60	486.61	
Dec-20	132183.00	1163.51	6981.13	0.00	124038.36	0.00	0.00	0.00	0.00	0.00	390.22	0.08	2.19	1.66	0.00	769.36	
Jan-21	78129.57	1315.84	4253.06	0.00	72560.67	0.00	0.00	0.00	0.00	0.00	393.38	0.05	2.68	1.96	0.00	917.77	
Feb-21	70013.03	912.17	10767.60	0.00	58333.26	0.00	0.00	0.00	0.00	0.00	386.46	0.07	1.24	0.64	0.00	523.76	
Mar-21	51743.65	1314.82	18740.08	0.00	31688.75	0.00	0.00	0.00	0.00	0.00	320.13	0.12	2.08	2.45	0.00	990.03	
Apr-21	16431.34	1411.19	0.00	0.00	15020.15	0.00	0.00	0.00	0.00	0.00	467.54	0.02	1.84	1.70	0.00	940.09	
May-21	39675.06	1610.42	0.00	0.00	38064.64	0.00	0.00	0.00	0.00	0.00	442.35	0.00	1.31	2.81	0.00	1163.95	
Jun-21	56589.31	1812.39	0.00	0.00	54776.92	0.00	0.00	0.00	0.00	0.00	353.07	0.02	1.10	1.37	0.00	1456.83	
Jul-21	18264.19	2544.22	0.00	0.00	15719.97	0.00	0.00	0.00	0.00	0.00	383.64	0.00	1.55	3.36	0.00	2155.67	
Aug-21	7959.53	2028.39	4150.75	0.00	1780.39	0.00	0.00	0.00	0.00	0.00	326.91	0.00	1.28	1.40	0.00	1698.80	
Sep-21	32389.58	2259.89	30129.69	0.00	0.00	0.00	0.00	0.00	0.00	0.00	269.75	0.00	1.99	2.68	0.00	1985.47	
Oct-21	34559.10	2034.74	17144.35	0.00	15380.01	0.00	0.00	0.00	0.00	0.00	289.21	0.00	1.04	2.83	0.00	1741.66	
Nov-21	34820.47	2352.98	6551.45	0.00	25916.04	0.00	0.00	0.00	0.00	0.00	164.09	0.00	1.27	3.80	0.00	2183.82	
Total	1295121.94	34264.93	176254.64	0.00	1084602.38	0.00	0.00	0.00	0.00	0.00	7132.72	0.75	29.54	53.63	4.20	27044.10	

Total C&D waste generated	1295121.94	tonne	a1=b+c+d+e+f+g+h+i+j+k+l+m
Total C&D waste generated (excluding excavated materials)	34264.93	tonne	a2=c+d+e+f+g+h+i+j+k+l+m
Total recycled C&D waste	7216.63	tonne	a3=c+d+e+h+i+j+k
% of recycled C&D waste for BEAM Plus MA10 or MA11	21.06	%	a4=a3/a2 x 100%

- Notes:
- (1) Metal, paper & plastic were collected by recycler.
  - (2) The performance target of waste recycling are specified in the Contract.
  - (3) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
  - (4) Plastics refer to plastic bottles/ containers, plastic/ foam from packaging material.
  - (5) Broken concrete for recycling into aggregates.
  - (6) Excavated materials/waste will NOT be considered as part of construction waste. It should be excluded in the calculation.
  - (7) Disposal of inert waste to public fill or sorting facilities will NOT be considered as recycled waste.
  - (8) Disposal record for October 2021 and November 2021 have been updated according to the latest information from contractor in November 2021.
  - (9) Recycling record for metals, papers and plastics have been updated according to the latest information from contractor in November 2021.

**Project: Proposed Composite Development at NKIL 6607, Shing Kai Road, Kai Tak, Kowloon**

**Company: Hip Hing Construction Co., Ltd.**

**Monthly Summary Waste Flow Table**

Month	Total Quantities Generated	Total Quantities Generated (excluded excavated material)	Accumulated Quantities of Inert C&D Materials Generated Monthly					Accumulated Quantities of Non-inert C&D Wastes Generated Monthly						
			(a)	(b)	(c)	(d)	(e)	(f)	(g)	(h)	(i)	(j)	(k)	(l)
			Broken Concrete Recycled	Broken Concrete Diverted to Public Fill	Excavated Materials Reused in this Project	Excavated Materials Reused in other Projects	Excavated Materials Disposed as Public Fill	Mixed Wastes Diverted to Sorting Facility	Metals Recycled	Paper/ Cardboard Packaging Recycled	Timber/Wood Pallet Recycled	Plastics Recycled	Chemical Waste Collected	Others, e.g. General Refuse Disposed at Landfill
			(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)	(in'000 kg)
Aug-21	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Sep-21	1550.68	0	0	0	0	1550.68	0	0	0	0	0	0	0	0
Oct-21	3681.12	17.35	0	0	0	3663.77	0	0	0	0	0	0	0	17.35
Nov-21	5434.59	39.01	0	0	0	5309.2	86.38	6.05	2.84	0	0	0	0	30.12
<b>Total</b>	<b>10666.39</b>	<b>56.36</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>10523.65</b>	<b>86.38</b>	<b>6.05</b>	<b>2.84</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>47.47</b>

Total C&D Waste generated 10666.39 Tons  
 Total C&D waste generated (Excluded excavated materials) 56.36 Tons  
 Total C&D waste recycled 2.84 Tons

$$\text{Waste Recycling Rate} = \frac{(a) + (g) + (h) + (i) + (j)}{(a) + (b) + (f) + (g) + (h) + (i) + (j) + (l)} \times 100\% = 5.04\%$$

Note:  
 For BEAM Plus certification scheme, excavated materials are excluded from the calculation of the waste reduction rate Record with Underlined indicated updated content

# Appendix J. Environmental Licences and Permits

**Table J.1: Summary of Environmental Licences and Permits Status (KTSP)**

Item No.	Type of Permit / Licence	Reference No.	Application Date	Valid from	Valid until	Remark
1	Environmental Permit under EIAO	EP-544/2017	21 Aug 2017	8 Sep 2017	N/A	Issued
2	Construction Dust Notification under APCO	441733	25 Jan 2019	29 Jan 2019	N/A	N/A
3	Construction Waste Disposal Account (Main)	7033182	12 Feb 2019	12 Feb 2019	N/A	N/A
4	Construction Waste Disposal Account (Vessel)	7033555	6 Oct 2021	25 Oct 2021	10 Feb 2022	Issued
5	Registration as a Chemical Waste Producer	WPN5213-286-H3906-02	29 Jan 2019	12 Feb 2019	N/A	N/A
6	Discharge Licence under WPCO	WT00034082-2019	12 Jun 2019	26 Jun 2019	30 Jun 2024	Issued
7	Construction Noise Permit (Percussive Piling)	PP-RE0015-21	13 May 2021	3 Jun 2021	23 Nov 2021	Issued
8	Construction Noise Permit (Construction Works, Barging Point)	GW-RE0378-21	12 Apr 2021	21 May 2021	10 Nov 2021	Superseded by GW-RE1034-21 on 11 Nov 2021
9	Construction Noise Permit (Construction Works, Southern Site)	GW-RE0833-21	11 Aug 2021	1 Sep 2021	28 Feb 2022	Issued
10	Construction Noise Permit (Construction Works, Northern Site)	GW-RE0890-21	10 Aug 2021	1 Nov 2021	31 Jan 2022	Issued
11	Construction Noise Permit (Special - Truss Delivery Port)	GW-RE0902-21	10 Sep 2021	15 Sep 2021	30 Nov 2021	Superseded by GW-RE1090-21 on 2 Nov 2021
12	Construction Noise Permit (Construction Works, Shing Kai Road)	GW-RE0929-21	17 Sep 2021	23 Sep 2021	3 Dec 2021	Issued

Item No.	Type of Permit / Licence	Reference No.	Application Date	Valid from	Valid until	Remark
13	Construction Noise Permit (Construction Works, Barging Point)	GW-RE1034-21	7 Oct 2021	11 Nov 2021	9 May 2022	Issued
14	Construction Noise Permit (Special Truss Delivery Port)	GW-RE1090-21	22 Oct 2021	2 Nov 2021	2 Feb 2022	Issued

**Table J.2: Summary of Environmental Licences and Permits Status (H/O Development)**

Item No.	Type of Permit / Licence	Reference No.	Application Date	Valid from	Valid until	Remark
1	Environmental Permit under EIAO	EP-544/2017	21 Aug 2017	8 Sep 2017	N/A	Issued
2	Construction Dust Notification under APCO	458255	17 Jul 2020	17 Jul 2020	N/A	N/A
		470045	29 Jul 2021	29 Jul 2021	N/A	N/A
3	Construction Waste Disposal Account (Main)	7041267	29 Jul 2021	11 Aug 2021	N/A	Issued
4	Registration as a Chemical Waste Producer	WPN5211-286-H1103-23	29 Jul 2021	24 Aug 2021	N/A	Issued
5	Discharge Licence under WPCO	WT00037364-2021	17 Jul 2020	22 Mar 2021	31 Mar 2026	Superseded by WT00039490-2021
		WT00039490-2021	6 Aug 2021	9 Nov 2021	30 Nov 2026	Issued
6	Marine Dumping Permit under DASO	EP/MD/21-087	23 Nov 2020	5 Jul 2021	4 Aug 2021	Issued
		470717 (Receipt No.)	18 Aug 2021	N/A	N/A	Pending
8	Construction Noise Permit	GW-RE1030-21	28 Sep 2021	21 Oct 2021	14 Apr 2022	Issued

# Appendix K. Environmental Mitigation Measures Implementation Status

## Air Quality – Recommended Mitigation Measures

Air Quality Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Good housekeeping to minimize dust generation, e.g. by properly handling and storing dusty materials	✓	✓
• Store cement in shelter with 3 sides and the top covered by impervious materials if the stack exceeds 20 bags	✓	✓
• Cement delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed	N/A	N/A
• Loading, unloading, transfer, handling or storage of bulk cement should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system	✓	N/A
• Dusty materials (e.g. debris) should be wetted by misting / water-spraying before any loading, unloading, transfer or transport operation	✓	✓
• Any skip hoist for material transport should be fully enclosed by impervious sheeting	✓	✓
• Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously	✓	✓
• Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities to maintain the entire surface wet	✓	✓
• Excavation area should be minimized as far as possible	✓	✓
• Stockpile of dusty materials should not be extended beyond the pedestrian barriers, fencing or traffic cones	✓	✓
• Excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet, and then removed, backfilled or reinstated where practicable within 24 hours of the excavation or unloading	P	✓
• Dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads	✓	✓
• Properly fitted side and tail boards are necessary for any vehicle with open load area	✓	✓
• While transporting materials that potentially create dust (e.g. debris), materials should not be loaded higher than side and tail boards, and should be fully covered by tarpaulin or similar materials which extend at least 300 mm over the edges of the side and tail boards to prevent leakage.	✓	✓
• Limit the maximum vehicle speed within the site to 10km/hr	✓	✓
• Haulage and delivery vehicles should be confined to designated roads	✓	✓
• Every main haul road should either be 1.) paved with concrete and kept clear of dusty materials, or 2.) sprayed or watered to maintain the entire road surface wet	✓	✓
• All on-site unpaved roads should be compacted and kept free of loose materials as possible	✓	✓
• Provide vehicle washing (e.g. wheel washing bay & high pressure water jet where practicable) at every vehicle exit point for cleaning vehicle body and wheels	✓	✓
• The vehicle washing area and the road between washing area and site exit should be paved with concrete, bituminous or other hardcores	✓	✓
• The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials.	✓	✓
• Dusty materials on every vehicle's body and wheels should be removed in washing area before leaving the site	✓	✓



Air Quality Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Regular maintenance of all plant equipment	✓	✓
• Throttle down or switch off unused machines or machine in intermittent use	✓	✓
• If the site is adjacent to area where accessible to the public (e.g. road and service lane etc.), hoarding of not less than 2.4 m high from ground level should be erected along the adjoining the entire length of that portion of the site boundary, except for a site entrance or exit. The hoarding should be well maintained throughout the construction period.	✓	✓
• Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding	✓	N/A
• Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies	✓	✓
• Carry out air quality monitoring throughout the construction period	✓	✓
• Carry out weekly site inspection to audit the implementation of mitigation measures	✓	✓
• Regular watering once per hour on exposed worksites and haul road with an equivalent intensity of not less than 1.3L/m <sup>3</sup> to achieve 91.7% dust removal efficiency.	P	P
• Provision of electrical vehicle (EV) charging facilities in at least one-third of the car parking spaces for private cars. Provision of EV charging enabling facilities in all car parking spaces provided for private cars.	✓	N/A
<b>Non-Road Mobile Machinery (NRMMS)</b>		
• All NRMMS operated on-site are approved or exempted (as the case may be) and affixed with the requisite approval/exemption labels under the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation or are in the process of application for such approval/exemption during the relevant grace period.	P	✓

## Noise – Recommended Mitigation Measures

Noise Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Adopt good site practice, such as throttle down or switch off equipment unused or intermittently used between works	✓	✓
• Regular maintenance of equipment to prevent noise emission due to impair	✓	✓
• Position mobile noisy equipment in locations away from NSRs and point the noise sources to directions away from NSRs	✓	✓
• Use silencer or muffler for equipment	✓	✓
• Make good use structures for noise screening	✓	✓
• Use Quality Powered Mechanical Equipment (QPME) and quiet equipment which produces lower noise level.	✓	✓
• Erect movable noise barrier of 3m height to shed large plant equipment (e.g. breaker, backhoe & mobile crane) or hand-held items (e.g. poker, wood saw, power rammer & compactor) near low-rise NSR. Where necessary, special design (e.g. with noise absorbing material or bend top) should be adopted. The barrier's length should be at least five times greater than its height, and the minimum surface density is 10 kg/m <sup>2</sup> . Alternatively, acoustic shed, enclosure or silencer (for generator, air compressor and concrete pump) or acoustic mat (for piling) can be adopted.	✓	N/A
• Carry out regular site inspection to audit the implementation of mitigation measures	✓	✓
• Carry out noise monitoring throughout the construction period	✓	✓

## Water Quality – Recommended Mitigation Measures

Water Quality Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Practices outlined in ProPECC PN 1/94 Construction Site Drainage should be adopted.	✓	✓
• Install perimeter channels in the works areas to intercept runoff from boundary prior to the commencement of any earthwork	✓	✓
• To prevent storm runoff from washing across exposed soil surfaces, intercepting channels should be provided.	✓	✓
• Drainage channels are required to convey site runoff to sand/silt traps and oil interceptors. Provision of regular cleaning and maintenance to ensure the normal operation of these facilities throughout the construction period.	✓	✓
• Any practical options for the diversion and realignment of drainage should comply with both engineering and environmental requirements	✓	✓
• Minimum distances of 100 m should be maintained between the discharge points of construction site runoff and the existing WSD saltwater intake and EMSD cooling water intake.	✓	✓
• The following good site measures should be adopted for the use of the existing barging facilities being operated by the MTR SCL Project: - All vessels should be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash. - All hopper barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material. - Construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site. - Loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water. - Barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation. Whole construction site Contractor P WPCO, EIAO-TM Page	N/A	N/A
• The runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS.	✓	✓
• Reuse and recycling of the treated effluent from construction site runoff.	✓	✓
• Weekly site audit should be carried out to check the implementation status of the recommended water quality impact mitigation measures throughout construction period.	✓	✓
• The construction programme should be properly planned to minimise soil excavation, if any, in rainy seasons.	✓	✓
• Any exposed soil surfaces should be properly protected to minimise dust emission.	✓	✓
• In areas where a large amount of exposed soils exist, earth bunds or sand bags should be provided.	✓	✓
• Exposed stockpiles should be covered with tarpaulin or impervious sheets at all times.	✓	✓
• The stockpiles of materials should be placed at locations away from any stream courses so as to avoid releasing materials into the water bodies.	✓	✓
• Final surfaces of earthworks should be compacted and protected by permanent work.	✓	✓
• Haul roads should be paved with concrete and the temporary access roads protected using crushed stone or gravel, wherever practicable.	✓	✓
• Wheel washing facilities should be provided at all site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles.	✓	✓
• Good site practices should be adopted to keep the site dry and tidy, such as clean the rubbish and litter on the construction sites.	✓	✓
• Adequate temporary site drainage and pumping should be provided, if necessary.	✓	✓
• Provide sufficient temporary toilets in the works areas. The toilet facilities should be more than 30 m from any watercourse. A licensed waste collector should be deployed to clean the temporary toilets on a regular basis.	✓	✓
• Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project.	✓	✓

Water Quality Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
<ul style="list-style-type: none"> <li>Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.</li> </ul>	✓	N/A
<ul style="list-style-type: none"> <li>Clean the construction sites on a regular basis.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Oil interceptor in car parking area shall be designed and constructed according to Practice Note for Authorized Persons, Registered Structural Engineers and Registered Geotechnical Engineers, APP-46 (PNAP 124)</li> </ul>	N/A	N/A
<ul style="list-style-type: none"> <li>Provide two sequential storage tanks to contain surface water with residual fertilizers and pesticides and third holding tank for incidental rainstorm</li> </ul>	N/A	N/A
<b>Sewerage and Sewage Treatment Implications</b>		
<ul style="list-style-type: none"> <li>Implementation of Sewer No. 1 and Sewer No.2 as proposed in Sections 7.2.2 - 7.2.3 of the EIA Report</li> </ul>	✓	✓

## Waste Management – Recommended Mitigation Measures

Waste Management Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
<ul style="list-style-type: none"> <li>Inert C&amp;D materials (or public fills) will be used to form the ramps and other filling area as far as civil engineering design permits.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>The contractor should formulate waste management measures on waste minimization, storage, handling and disposal in a Waste Management Plan as part of Environmental Management Plan.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Adopt good site practice as follows:                             <ul style="list-style-type: none"> <li>Provide training to workers on site cleanliness, waste management (waste reduction, reuse and recycle) and chemical handling procedures</li> <li>Provide sufficient waste collection points and regular removal</li> <li>Cover waste materials with tarpaulin or in enclosure during transportation</li> <li>Maintain drainage systems, sumps and oil interceptors</li> <li>Sort out chemical waste for proper handling and treatment onsite or offsite</li> </ul> </li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Adopt waste reduction measures as follows:                             <ul style="list-style-type: none"> <li>Allocate area/containers for sorting, recovering and storing waste for reuse, recycle or disposal (e.g. demolition debris and excavated materials, general refuse like aluminium cans.) Remove waste from the Site for sorting once generated if no suitable space can be identified.</li> <li>Allocate area for proper storage of construction materials to prevent contamination</li> <li>Minimize wastage through careful planning and avoiding over-purchase of construction materials</li> </ul> </li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Store waste materials properly as follows:                             <ul style="list-style-type: none"> <li>Avoid contamination by proper handling and storing waste</li> <li>Prevent erosion by covering waste</li> <li>Apply water spray on excavated materials</li> <li>Maintain and clean storage area regularly</li> <li>Sort and stockpile different materials at designated location to enhance reuse</li> </ul> </li> </ul>	P	✓
<ul style="list-style-type: none"> <li>Apply for relevant waste disposal permits in accordance with the Waste Disposal Ordinance (Cap. 354), Waste Disposal (Charges for Disposal of Construction Waste) Regulation (Cap. 345) and the Land (Miscellaneous Provisions) Ordinance (Cap. 28), Dumping at Sea Ordinance (Cap. 466).</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Hire licensed waste disposal contractors for waste collection and removal. Dispose waste at licensed waste disposal facilities.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Implement trip-ticket system for recording the amount of waste generated, recycled and disposed, including chemical wastes</li> </ul>	✓	✓

Waste Management Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
<ul style="list-style-type: none"> <li>Reduce water content in wet spoil generated from piling work by mixing with dry materials. Only dispose treated spoil with less than 25% dry density to Public Fill Reception Facilities</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Dispose dry waste or waste with less than 70% water content by weight to landfill</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Follow the Code of Practice on the Packaging, Labelling and Storage of Chemical Waste as follows:                             <ul style="list-style-type: none"> <li>Store chemical wastes with suitable containers. Seal and maintain the container to avoid leakage or spillage during storage, handling and transport</li> <li>Label chemical waste containers in both English and Chinese with instructions in accordance to Schedule 2 of the Waste Disposal (Chemical Waste) (General) Regulation</li> <li>The container capacity should be smaller than 450 litres unless agreed by the EPD</li> </ul> </li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Comply with the requirement of the chemical storage area:                             <ul style="list-style-type: none"> <li>Store only chemical waste and label clearly the chemical characters of the waste</li> <li>Have at least 3 sides enclosed and protected from rainfall with cover</li> <li>Provide sufficient ventilation</li> <li>Have impermeable floor and has bunds to contain 110% of the capacity of the largest container or 20% of the total volume of the stored waste in the area, whichever is larger</li> <li>Adequately spaced incompatible materials</li> </ul> </li> </ul>	P	P
<ul style="list-style-type: none"> <li>Transfer used lubricants, waste oils and other chemicals to oil recycling companies, if possible, and empty oil drums for reuse or refill. No direct or indirect discharge is permitted</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Hire licensed chemical waste disposal contractors for waste collection and removal. Dispose chemical waste at the approved Chemical Waste Treatment Centre at Tsing Yi or other licensed facility</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Hire reputable waste collector to separately collect and dispose general refuse from other wastes. Cover the waste to prevent being blown away</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>The hauling of C&amp;D materials shall follow established environmental mitigation measures as stated in Practice Note for Registered Contractors No. 17 "Control of Environmental Nuisance from Construction Sites" issued by the Buildings Department</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Provide recycling bins for sorting out recyclables for collection by recycling companies. Non-recyclables should be removed to designated landfills every day by licensed collectors to prevent environmental and health nuisance.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Organize training and reminders to site staff on waste minimization through avoidance and reduction, reusing and recycling</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Bentonite slurry which will not be reused shall be disposed of from the Site as soon as possible. Residual used dewatered bentonite slurry should be disposed to a public filling area and liquid bentonite slurry if mixed with inert fill material should be disposed to a public filling area.</li> </ul>	N/A	N/A
<ul style="list-style-type: none"> <li>If chemical wastes were to be produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer, and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the waste such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport the chemical wastes.</li> <li>The licensed collector shall deliver the waste to the Chemical Waste Treatment Centre at Tsing Yi, or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>Carry out weekly site inspection to check the implementation status of the recommended waste management measures.</li> </ul>	✓	✓
<ul style="list-style-type: none"> <li>The barging of C&amp;DM for this Project shall use the existing Kai Tak Barging Facility (KTBF), or otherwise approved by the Director.</li> </ul>	N/A	N/A

## Ecology – Recommended Mitigation Measures

Ecology Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Erection of hoarding, fencing or provision of clear demarcation of work zone	✓	✓
• Designate areas for placement of equipment, building materials and wastes away from drainage channels	✓	✓
• Carry out weekly site inspection to check the implementation status and the effectiveness of the proposed mitigation measures	✓	✓

## Landscape and Visual – Recommended Mitigation Measures

Landscape and Visual Mitigation Measures during construction	Implementation Status	
	KTSP	H/O
• Construction Lighting Control - All security floodlights for construction sites should be equipped with adjustable shields, frosted diffusers and reflective covers, and be controlled to minimize light pollution and night-time glare to the visual sensitive receivers (VSRs).	✓	N/A
• Temporary Landscape Treatments - Including vertical greening, pot planting and application of green roofing to site offices, Hydroseeding of site formation areas and short term greening of site boundaries and land not immediately developed.	✓	N/A
• Decoration of Hoarding - Erection of screen hoardings should be designed appropriately to be compatible with the existing urban context, either brightly and imaginatively or with visually unobtrusive design and colours where more appropriate.	✓	✓
• All security floodlights for construction sites shall be equipped with adjustable shield, frosted diffusers and reflective covers, and be carefully controlled to minimize light pollution and night-time glare to nearby receivers	✓	N/A
• Site inspection should be undertaken once every two weeks.	✓	✓
• Compensatory Tree Planting - A new parkland area is created in the project development to be used for the implementation of compensatory tree planting to offset the net loss of key landscape resources. It is recommended that 340 trees be planted in this regard and a compensatory tree planting proposal outlining the locations of tree compensation will be submitted separately in seeking relevant government department's approval in accordance with DEVB TC No.7/2015.	N/A	N/A

## Other – Recommended Mitigation Measures

• Relevant environmental permits/licences should be posted at all vehicle entrances/exits.	✓	✓
--------------------------------------------------------------------------------------------	---	---

### Legend:

✓	Implemented
×	Not implemented
P	Partially implemented
N/A	Not applicable

## Appendix L. Statistics on Environmental Complaints, Notification of Summons and Successful Prosecutions

**Table L.1: Statistics on Environmental Complaints, Notifications of Summons and Successful Prosecutions**

Reporting Period	Complaints	Notifications of Summons	Successful Prosecutions
This reporting period (Nov 2021)	2	0	0
From commencement data of construction to end of reporting month	18	0	0

# Appendix M. Complaint Investigation Report

### Complaint Investigation Report

RECEIPT OF COMPLAINT		Ref: COM_0017
Date:	1 November 2021	
Time:	15:06	
From:	PS Chan (Hip Hing Construction Co., Ltd)	
Via:	Email	
Contact no.:	-	
COMPLAINANT		
Name:	-	Address: -
Contact no.:	-	
DETAILS OF COMPLAINT		
Date:	31 October 2021	
Time:	-	
Parameter:*	<del>Dust</del> Noise <del>Water</del> Other (specify):	
Description:	<p>- Complaint of noise nuisance arising from the truss delivery operation in nighttime affecting the residents of the Grand Waterfront.</p> <p>- Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit.</p> <p>- Please take necessary measures to minimize the environmental nuisance arising from the construction site.</p>	
INVESTIGATION RESULT & RESPONSE		
ET, IEC and SOR notified on:	1 November 2021	
Investigation conducted on:	2 and 3 November 2021	
Result of investigation:	<p>Complaint investigation was carried out on 2 and 3 November 2021, the results of investigation were summarized as following:</p> <p>According to the complaint information, the concerned residential building was located at Grand Waterfront. (See attached location plan)</p> <p>According to the contractor information, there were no truss delivery work conducted on the complaint date (i.e. 31 October 2021.) There were two nighttime truss delivery works carried out during the concerned week under the Construction Noise Permit (Ref. No. GW-RE0902-21) requirement:</p> <p><b>(i) 29 October 2021, 20:00– 00:00; and (ii) 30 October 2021, 20:00-00:00</b></p> <p>Noise mitigation control measures implemented on site included:</p> <ol style="list-style-type: none"> <li>Noise barrier not less than 2m had been provided on site between the truss delivery working area and the Grand Waterfront according to the CNP requirement. (photos 1a and 1b)</li> <li>Noise insulating fabric implemented on moving trailer during nighttime truss delivery work. (photos 2a and 2b)</li> </ol> <p>In conclusion, noise control mitigation measures at the truss delivery port have been well implemented. All nighttime truss delivery operation works have been fulfilling the relevant environmental legislation and CNP requirement during the concerned period. The contractor was reminded to maintain all necessary noise mitigation measures to minimise any potential noise nuisance to nearby residential during the nighttime truss delivery operation.</p>	
RECOMMENDATIONS / MITIGATION MEASURES / ACTIONS		
<p>Environmental mitigation measures have been maintained as follow:</p> <ol style="list-style-type: none"> <li>The truss delivery works have been scheduled in the daytime as much as practicable to minimise the noise nuisance at nighttime. (photo 3)</li> <li>Advance notification of nighttime truss delivery work has been issued to nearby residential according to the CNP requirement. (photo 4)</li> </ol>		



3. Pre work briefing has been provided to ensure the compliance of CNP requirement to minimise potential noise nuisance during the truss delivery. (photo 5)

Prepared by: Sunny Chan Title: Environmental Team Leader

Signature:  Date: 8 November 2021

**Attachment:**

- 1. Record of Construction Noise Permit - GW-RE0902-21**
- 2. Location Plan of the KTSP Truss Delivery Boundary**
- 3. Photo Records**

本署檔案  
OUR REF : (5) in EP631/K10/RE470967-21  
來函檔案  
YOUR REF :  
電話  
TEL NO : 2150 8081  
圖文傳真  
FAX NO : 2402 8275  
網址  
HOMEPAGE : <http://www.epd.gov.hk/>

Environmental Protection Department  
Environmental Compliance Division  
Regional Office (East)  
8/F., Cheung Sha Wan Government Offices,  
303 Cheung Sha Wan Road,  
Kowloon



環境保護署  
環保法規管理科  
區域辦事處(東)  
九龍長沙灣道303號  
長沙灣政府合署8樓

Registered Post

10 September 2021

To: HIP HING ENGINEERING COMPANY LIMITED  
11/F., Chevalier Commercial Centre,  
8 Wang Hoi Road,  
Kowloon Bay,  
Kowloon

Dear Sir,

**Advance notification to nearby residents in respect of works  
at Construction site of Kai Tak Sports Park (truss delivery port), Kai Tak, Kowloon  
under Construction Noise Permit No. GW-RE0902-21**

In connection with our Notice of Issue ref. (4) in EP631/K10/RE470967-21 dated 10 September 2021 of the captioned construction noise permit, please be advised that the permit was issued under a consideration of unavoidable constraints on working hours at the construction site concerned. Notwithstanding the noise control measures specified in the permit, the noise produced by the works is expected to exceed the statutory noise limit, thus causing disturbance to the nearby residents. This may result in noise complaints which may affect the image of your company.

As a measure to alert the affected persons, and to help maintain good public relations and reduce noise complaints, you are strongly advised to notify the nearby residents by providing details such as dates and hours of operation, location and nature of works, and contact telephone numbers to them a few days in advance of the construction. A sample notice to be posted to residential building notice boards is attached for your use. Please also send a copy of the notice to the undersigned by facsimile for our information a few days prior to the commencement of the construction.

Your cooperation in this matter is highly appreciated.

Yours faithfully,

(TANG Wai-man, Lisa)  
Environmental Protection Officer  
for Director of Environmental Protection

c.c. Home Affairs Bureau  
[Attn: Mr. XU Wei Hao (E(RS))]  
(Fax no. 3586 0591)

(5) in EP631/K10/RE470967-21

2150 8081

2402 8275

掛號函件

致： 九龍 九龍灣  
宏開道 8 號  
其士商業中心 11 樓  
協興工程有限公司

執事先生：

**根據「建築噪音許可證第 GW-RE0902-21 號」**  
**於九龍啟德啟德體育園的建築地盤(桁架卸貨港)進行工程前預先知會附近居民**

本辦事處在二零二一年九月十日發信(檔號(4) in EP631/K10/RE470967-21)通知你，上述「建築噪音許可證」已經發出，就此再函說明，我們是鑑於貴方在有關工地的施工時間難免受限制，因而簽發該許可證。儘管許可證上已列各項噪音控制措施，但工程產生的噪音，預計仍會超出法定噪音規限，滋擾鄰近住戶，或有可能引起噪音滋擾投訴，影響貴公司的形象。

為方便受影響的人士察覺有關的情況，並保持良好的公共關係，減少噪音滋擾投訴，本處籲請你在施工前數天知會鄰戶，說明工程的詳情，例如進行工程的日期和時間、工程的地點和性質，以及查詢的電話號碼。隨函夾附可供在住宅大廈告示板上張貼的告示式樣，以供參考。此外，請在進行工程前數天，以傳真方式交來告示副本備閱。

多謝合作。

環境保護署署長

(鄧慧敏



代行)

副本送： 民政事務局  
[經辦人：徐維浩 先生(工程師(康樂及體育))]  
(傳真號碼：3586 0591)

二零二一年九月十日

Notice to Affected Residents  
(SAMPLE)

(DATE)

Dear Residents,

I am writing to let you know that we will be carrying out \_\_\_\_\_  
\_\_\_\_\_ in the vicinity of  
(Nature of works : e.g. drainage maintenance works)  
\_\_\_\_\_ during the  
(Location : e.g. XYZ Street between ABC Road and DEY Road)  
hours of \_\_\_\_\_ from \_\_\_\_\_ to \_\_\_\_\_.  
(e.g. 10:00 pm to 1:00 am) (Period : e.g. 15 January 2015 to 18 January 2015)

I wish to apologize for the inconvenience that this may cause you while I am sure you will understand that such works are an integral part of providing essential services to you and other residents in your neighbourhood.

You may like to note that it is not possible for us to conduct the works during the day time hours due to \_\_\_\_\_.  
(Reasons : e.g. traffic conditions)

Please be assured that we will carry out the works as quickly as possible with due regard to the noise intrusion which may result. We will also be adopting noise mitigation measures such as \_\_\_\_\_.  
(e.g. low noise generator enclosed by an acoustical enclosure)

If you have any enquiries regarding the works, please feel free to contact our \_\_\_\_\_  
(Representative : e.g. works supervisor, Mr. A.B. Cee at Mobile Phone or Pager No. or Mr. E.F. Gee, engineer at Phone : xxxx-yyyy)

Yours truly,

(NAME)  
(POST)  
(NAME OF COMPANY)

c.c. EPD (Attn.: CI(RE)5 - Fax No.: 2756 8588)

致受影響居民的通知書

(樣本)

各位居民：

現來信通知由\_\_\_\_年\_\_月\_\_日至\_\_\_\_年\_\_月\_\_日\_\_\_\_時至\_\_\_\_時在  
(時期: 例如 2015年1月15日至2015年1月18日 (例如晚上10時至零晨1時))

\_\_\_\_\_  
(位置: 例如 ABC 道與 DEF 道之間的 XYZ 街)

附近進行\_\_\_\_\_。  
(工作性質: 例如 排水渠維修工程)

本公司對因這些工程造成的不便表示歉意，而深信閣下明白這些工程是為閣下及其他鄰近居民提供重要服務中的重要一環。

在日間由於\_\_\_\_\_，本公司無法進行上述工程，  
(理由: 例如交通情況)

但本公司保證盡快進行上述工程，並注意可能造成的噪音。本公司亦會採取噪音舒緩措施如\_\_\_\_\_。  
(例如由隔聲圍封物圍封低噪音產生器)

如對上述工程有任何疑問，請聯絡\_\_\_\_\_ [代表: 例如工程主管, ABC 先生 (手提

電話號碼或傳呼號碼) 或工程師 EFG 先生，電話號碼，xxxx-yyyy]

\_\_\_\_\_  
公司名稱

\_\_\_\_\_  
職位

\_\_\_\_\_  
姓名

副本送：環境保護署 (CI(RE)5 - 傳真號碼: 2756 8588)

本署檔案  
OUR REF : (4) in EP631/K10/RE470967-21  
來函檔案  
YOUR REF :  
電話  
TEL NO : 2150 8081  
圖文傳真  
FAX NO : 2402 8275  
網址  
HOMEPAGE : <http://www.epd.gov.hk/>

Environmental Protection Department  
Environmental Compliance Division  
Regional Office (East)

8/F., Cheung Sha Wan Government Offices,  
303 Cheung Sha Wan Road,  
Kowloon



環境保護署  
環保法規管理科  
區域辦事處(東)  
九龍長沙灣道 303 號  
長沙灣政府合署 8 樓

Registered Post

10 September 2021

To: HIP HING ENGINEERING COMPANY LIMITED  
11/F., Chevalier Commercial Centre,  
8 Wang Hoi Road,  
Kowloon Bay,  
Kowloon

Dear Sir,

**Notice of Issue of Construction Noise Permit pursuant  
to section 8(6) of the Noise Control Ordinance (Cap. 400)**

I write to inform you that, under section 8(6) of the Noise Control Ordinance, the Authority has decided to issue a construction noise permit in respect of your application, which was received by the Authority on 25 August 2021, **for the use of powered mechanical equipment for carrying out construction work at Construction site of Kai Tak Sports Park (truss delivery port), Kai Tak, Kowloon.**

The construction noise permit No. GW-RE0902-21 is enclosed.

Please note that a condition concerning **online submission of advance notification of work** to the Authority has been incorporated into this construction noise permit. You are strongly advised to read the conditions of the permit carefully and to ensure compliance with these conditions. Any breaching of the conditions may lead to cancellation of the permit, **subsequent prosecution action** and/or the Authority's refusal to issue further permit for the above construction site.

Yours faithfully,

(TANG Wai-man, Lisa)  
for Authority

Note:

Electronic submission of application for construction noise permit is available at Environmental Protection Department's website. File attachments with total size not exceeding 20 MB in acceptable format are allowed for electronic submission. Electronic application form can be downloaded from our website (<https://epic.epd.gov.hk/eForm/ChangeLanguage.do?language=eng&url=/pages/datadownload/downloadMain.jsp>) and an overview of application submission (<https://epic.epd.gov.hk/eForm/introduce.html>) is provided for more information.

(4) in EP631/K10/RE470967-21

2150 8081

2402 8275

掛號函件

致： 九龍·九龍灣  
宏開道 8 號  
其士商業中心 11 樓  
協興工程有限公司

執事先生：

根據《噪音管制條例(第 400 章)》第 8(6)條  
發出的通知書 — 簽發「建築噪音許可證」

本監督於二零二一年八月二十五日，收到你擬於下述地址：九龍啟德啟德體育園的建築地盤(桁架卸貨港)，使用機動設備進行建築工程而提出的「建築噪音許可證」申請，現根據《噪音管制條例》第 8(6)條的規定通知你，上述的申請已被批准。

隨函附上「第 GW-RE0902-21 號建築噪音許可證」。

請注意，有關**施工前於網上預先通知**本監督的要求已納入本建築噪音許可證的條件。請細閱及確保遵守許可證各項條件。如有違反，本監督可撤銷許可證、**提出檢控及/或拒絕再就上述地盤簽發任何「建築噪音許可證」**。

監 督

(鄧慧敏



代行)

二零二一年九月十日

注意：

環境保護署提供網上申請「建築噪音許可證」服務。網上申請容許上傳檔案總容量不大於 20 MB 的有關文件。可於本署網頁下載電子表格

(<https://epic.epd.gov.hk/eForm/ChangeLanguage.do?language=eng&url=/pages/datadownload/downloadMain.jsp>)及參閱電子表格提交服務概覽(<https://epic.epd.gov.hk/eForm/introduce.html>)，了解更多資料。

表格 3  
 噪音管制條例  
 (第400章)  
 第8(9)條

建築噪音許可證  
 為進行建築工程（撞擊式打樁除外）  
 而使用機動設備及／或進行訂明建築工程

建築噪音許可證編號： GW-RE0902-21

致： 協興工程有限公司

本建築噪音許可證是按照《噪音管制條例》第8條的規定而發出的。現准予使用機動設備以進行撞擊式打樁工程以外的建築工程及／或進行訂明建築工程，但須受以下條件規限。若不按照該等條件進行建築工程，許可證可遭撤銷，而且會受到檢控。

條 件

1. 可使用機動設備及／或進行訂明建築工程的建築地盤：

詳細地址：九龍啟德啟德體育園的建築地盤(桁架卸貨港)。

地段編號：---

地盤範圍(即可使用機動設備及進行訂明建築工程的地方範圍)已描劃於夾附的圖則上，而該圖則是本建築噪音許可證的一部分。

2. 該地盤部分／全部\*位於指定範圍之內／外\*。

3. 機動設備

- a. 在地盤範圍內可使用的各項機動設備：

各項機動設備的識辨代碼 (如適用的話)	各項機動設備的說明	數目
<u>A組</u> ---	自行式拖車	陸
---	發電機，備有優質機動設備標籤顯示聲功率級≤94分貝(A)	壹
<u>B組</u> CNP 048	起重機，流動(油渣)	壹
---	發電機，備有優質機動設備標籤顯示聲功率級≤94分貝(A)	壹
---	平頂躉船	壹
CNP 221	拖船	壹

- b. 可使用機動設備的建築噪音許可證有效期：

生效日期及時間：二零二一年九月十五日 下午七時

日期及時間：公眾假日(包括星期日)的凌晨零時至晚上十二時，公眾假日以外的任何一日凌晨零時至上午七時及下午七時至晚上十二時。

此部分許可證屆滿日期及時間：二零二一年十一月三十日 晚上十二時

日期

時間

- c. 建築地盤須備有本建築噪音許可證所述每件機動設備的照片各一幀，供監督隨時查看；該等照片須經監督認可。

- d. 規限使用機動設備的其他條件：

請參見附頁有關本建築噪音許可證的規限條件。該條件是鑒於本建築噪音許可證屬特別個案而註明的，而該特別個案是施工時段受潮汐限制。



4. 訂明建築工程

a. 在地盤範圍內可進行的訂明建築工程：

訂明建築工程的識辨代碼	訂明建築工程的類別的說明
	不適用

b. 可進行訂明建築工程的建築噪音許可證有效期：

生效日期及時間：不適用.....

日期及時間：不適用.....

此部分許可證屆滿日期及時間：.....不適用.....

c. 本許可證可夾附經監督認可的地盤圖則，以顯示本許可證准予進行訂明建築工程的點。該地盤圖則須存放於建築地盤供監督隨時查看。  
日期 時間

d. 規限進行訂明建築工程的其他條件：

.....  
.....  
.....

5. 本建築噪音許可證或其副本必須展示於建築地盤的所有車輛入口處，給予公眾人士參閱。

.....  
.....

日期：2021 年 09 月 10 日



簽署：.....

監督  
(鄧慧敏 代行)

\* 刪去不適用者

FORM 3  
NOISE CONTROL ORDINANCE  
(Chapter 400)  
SECTION 8(9)

[reg.5(a)]

**CONSTRUCTION NOISE PERMIT FOR THE USE OF POWERED  
MECHANICAL EQUIPMENT FOR THE PURPOSE OF CARRYING OUT  
CONSTRUCTION WORK OTHER THAN PERCUSSIVE PILING AND/OR  
THE CARRYING OUT OF PRESCRIBED CONSTRUCTION WORK**

CONSTRUCTION NOISE PERMIT NO. GW-RE0902-21

To : HIP HING ENGINEERING COMPANY LIMITED

This construction noise permit is issued in accordance with section 8 of the Noise Control Ordinance. Permission is granted for the use of powered mechanical equipment for the purpose of carrying out construction work other than percussive piling and/or the carrying out of prescribed construction work, subject to the conditions set out below. The carrying out of construction work otherwise than in accordance with the conditions may result in the permit being cancelled and in a prosecution for an offence.

*CONDITIONS*

1. Construction site where the powered mechanical equipment and/or prescribed construction work may be employed:

Full address: Construction site of Kai Tak Sports Park (truss delivery port), Kai Tak, Kowloon.

Lot No.: ---

The site boundary, that is, the boundary of the area within which the powered mechanical equipment may be used and the prescribed construction work may be carried out is delineated on the attached plan which forms part of this construction noise permit.

2. \* PART/WHOLE of the site falls \* WITHIN/OUTSIDE a designated area.

3. Powered Mechanical Equipment

- a. Items of powered mechanical equipment which may be used inside the site boundary :

<i>Identification code of item of powered mechanical equipment (if applicable)</i>	<i>Description of item of powered mechanical equipment</i>	<i>No. of units</i>
<b>Group A</b> ---	Self-propelled trailer	Six
---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level $\leq 94$ dB(A)	One
<b>Group B</b> CNP 048	Crane, mobile (diesel)	One
---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level $\leq 94$ dB(A)	One
---	Flat top barge	One
CNP 221	Tug boat	One

- b. Validity of the construction noise permit for the use of the powered mechanical equipment:

Date and time of commencement : 15 September 2021 at 1900 hours

Days and hours : 0000-2400 hours on general holidays (including Sundays), 0000-0700 hours and 1900-2400 hours on any day not being a general holiday.

This part of the permit expires on : 30 November 2021 at 2400 hours

- c. One photograph, endorsed by the Authority, of each item of powered mechanical equipment described in this construction noise permit is required to be kept on the construction site and made available for inspection by the Authority.

- d. Other conditions imposed on the use of the powered mechanical equipment:

Please refer to attached sheet for conditions imposed for this construction noise permit which is issued as a **special case** due to constraints on working hours governed by tidal conditions.

4. Prescribed Construction Work

a. Type of prescribed construction work which may be carried out inside the site boundary:

<i>Identification code of type of prescribed construction work</i>	<i>Description of type of prescribed construction work</i>
	Not applicable

b. Validity of the construction noise permit for the carrying out of the prescribed construction work:

Date and time of commencement : Not applicable at Not applicable

Date and hours : Not applicable

This part of the permit expires on : Not applicable at Not applicable

c. ~~Site layout plan(s), endorsed by the Authority, may be attached with the permit to indicate the locations permitted for the carrying out of prescribed construction work described in this permit. The layout plan(s) is(are) required to be kept on the construction site and made available for inspection by the Authority.~~

d. Other conditions imposed on the carrying out of the prescribed construction work:

\_\_\_\_\_

\_\_\_\_\_

\_\_\_\_\_

5. This construction noise permit or a copy thereof must be displayed on the construction site at all vehicular entrances for public information.

Dated this 10<sup>th</sup> day of September 2021

Signed :



(TANG Wai-man, Lisa)  
for Authority

\* Delete as necessary

**Sheet attached to Construction Noise Permit  
No. GW-RE0902-21**

3.d. Other conditions imposed on the use of the powered mechanical equipment:

1. The powered mechanical equipment shall not be used more than **10 days** during the validity period of this Construction Noise Permit.
2. All care shall be taken to ensure that the construction work is carried out as quickly as possible with due regard for the potential noise intrusion which may result.
3. Only one group of the powered mechanical equipment listed in condition 3.a shall be allowed to operate at any time.
4. The mobile crane (diesel) (CNP 048) shall be operated at the location as marked on the attached plan.
5. The power generating part of Self-propelled trailer shall be enclosed by a canvas acoustic shroud of vinyl sheets or equivalent.
6. Noise barrier with minimum 2 metres high shall be installed at the location as marked on the attached plan.
7. The powered mechanical equipment covered by this Construction Noise Permit shall not be operated when any powered mechanical equipment covered by the Construction Noise Permit No. GW-RE0598-21 and GW-RE0833-21 is being operated.
8. All flaps and panels of the generator shall be closed during operation.
9. All idling powered mechanical equipment shall be switched off.
10. Portable phones or walkie-talkies with headphones shall be used for site communication. No whistles, horns and loudspeakers shall be used. No shouting shall be allowed.
11. The construction work in relation to this Construction Noise Permit shall only be carried out with prior notification to the Authority of the location, date and time of the work as well as the details of work program (including the date and time for carrying out different phases or sequence of work ) etc. Such notification shall be made by logging in the following webpage (<http://cnp-advancenotification.hk>) and submitting all information required. Such notification shall be made within 14 days but no less than 48 hours before commencement of work for every work location.

Signed : \_\_\_\_\_



(TANG Wai-man, Lisa)  
for Authority

建築噪音許可證  
編號 GW-RE0902-21 的附頁

3. d. 規限使用機動設備的其他條件：

1. 祇可在此建築噪音許可證的有效期內使用機動設備不超過十天。
2. 本許可證持有人必須確保竭力從速完成該等建築工程，並小心防範會引起的噪音干擾。
3. 在任何時間內，祇可使用列在條件 3. a 內的其中一組機動設備。
4. 流動起重機(油渣) (CNP 048)必須在附圖上標示的位置操作。
5. 自行式拖車的動力產生部份必須用合成隔音屏障或同等物料圍封。
6. 必須在附圖上標示的位置上裝設高度不低於 2 米的隔音屏障。
7. 當建築噪音許可證編號 GW-RE0598-21 及 GW-RE0833-21 內的任何機動設備正在操作時，不可操作本建築噪音許可證內的機動設備。
8. 發電機的所有覆蓋及嵌板於操作時必須關閉。
9. 關掉所有空轉的機動設備。
10. 地盤通訊必須使用手提電話或連耳筒對講機，不准使用哨子、號角及擴音器，不准喧嘩。
11. 在進行此建築噪音許可證內所載列的建築工程時，必須確保就每個施工地點於施工前 48 小時至施工前 14 日內，登入以下網上平台 (<http://cnp-advancenotification.hk/tc>) 並就每個施工地點於施工前 48 小時至施工前 14 日內填妥及提交有關施工地點、日期及時間、及施工程序安排(包括不同階段或工序施工日期及時間的安排)等所需資料。



簽署：\_\_\_\_\_

監督  
(鄧慧敏 代行)

**Photograph(s) attached to Construction Noise Permit No. GW-RE0902-21**  
**建築噪音許可證編號：GW-RE0902-21 的照片**




Self-propelled trailer  
自行式拖車



CNP 048 Crane, mobile (diesel)  
起重機，流動(油渣)

**Photograph(s) attached to Construction Noise Permit No. GW-RE0902-21**  
**建築噪音許可證編號：GW-RE0902-21 的照片**

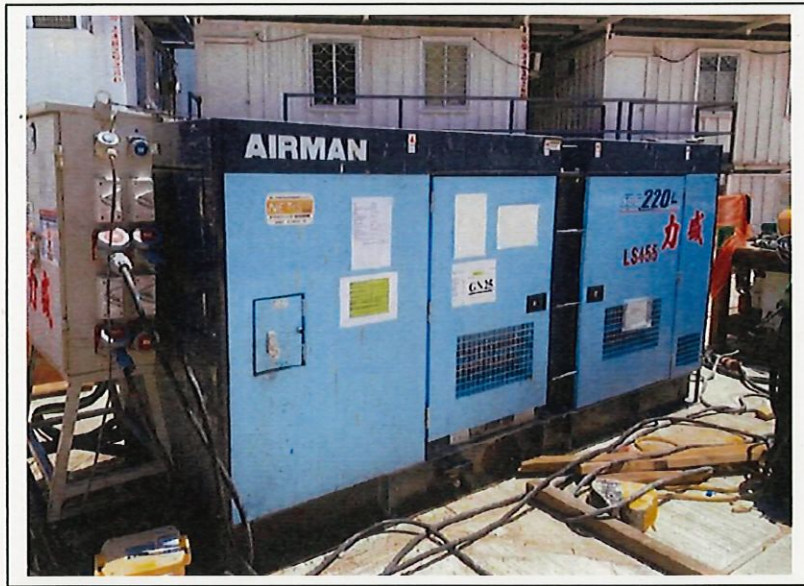

Generator, with Quality Powered Mechanical Equipment Label  
showing a Sound Power Level  $\leq 94$  dB(A)  
發電機，備有優質機動設備標籤顯示聲功率級  $\leq 94$  分貝(A)



Noise barrier  
隔音屏障



Photograph(s) attached to Construction Noise Permit No. GW-RE0902-21

建築噪音許可證編號：GW-RE0902-21 的照片



Flat top barge

平頂躉船



CNP 221 Tug boat


拖船







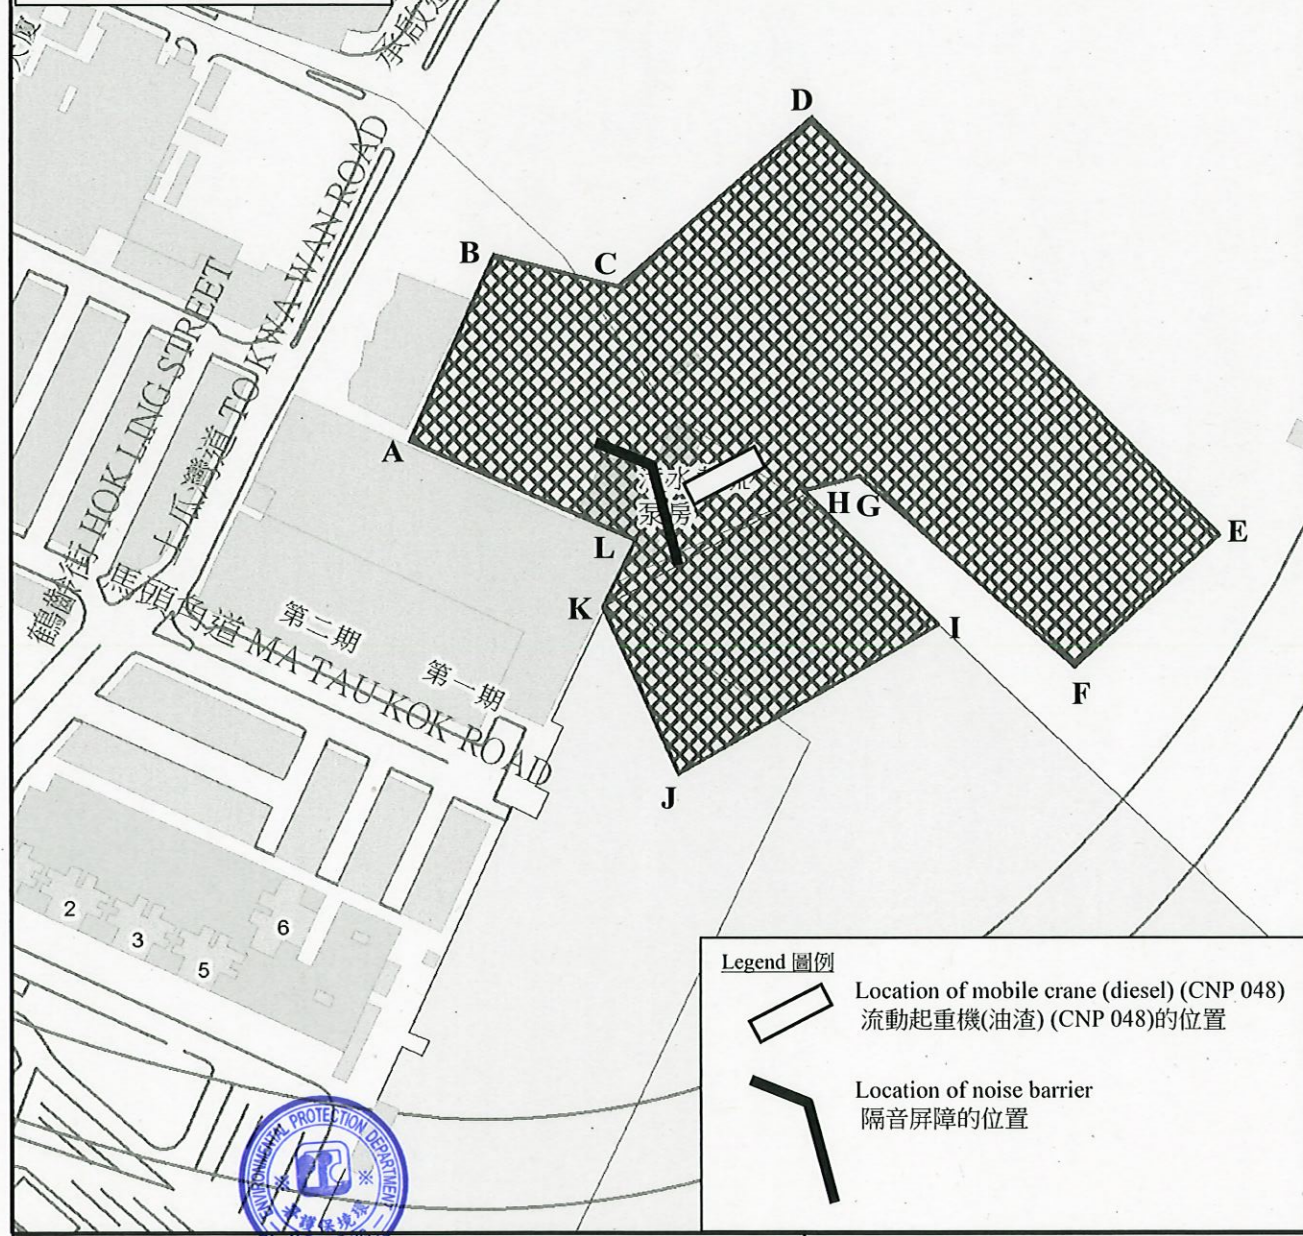

Location of Construction Site 建築地盤的位置		
Location	Northing	Easting
A	820216	838085
B	820291	838119
C	820278	838168
D	820346	838245
E	820178	838407
F	820125	838350
G	820202	838264
H	820196	838242
I	820142	838295
J	820082	838192
K	820149	838162
L	820176	838175



**Legend 圖例**

 Location of mobile crane (diesel) (CNP 048)  
流動起重機(油渣) (CNP 048)的位置

 Location of noise barrier  
隔音屏障的位置


環境保護署  
Environmental Protection Department Noise Control Authority

噪音管制監督


圖例 Legend  
 建築地盤 Construction Site

建築噪音許可證編號 GW-RE0902-21 的附圖  
Plan attached to Construction Noise Permit No. GW-RE0902-21

比例 Scale 1:3,000

 米 Meters  
0 15 30 60 90

### Location Plan of the KTSP Truss Delivery Boundary

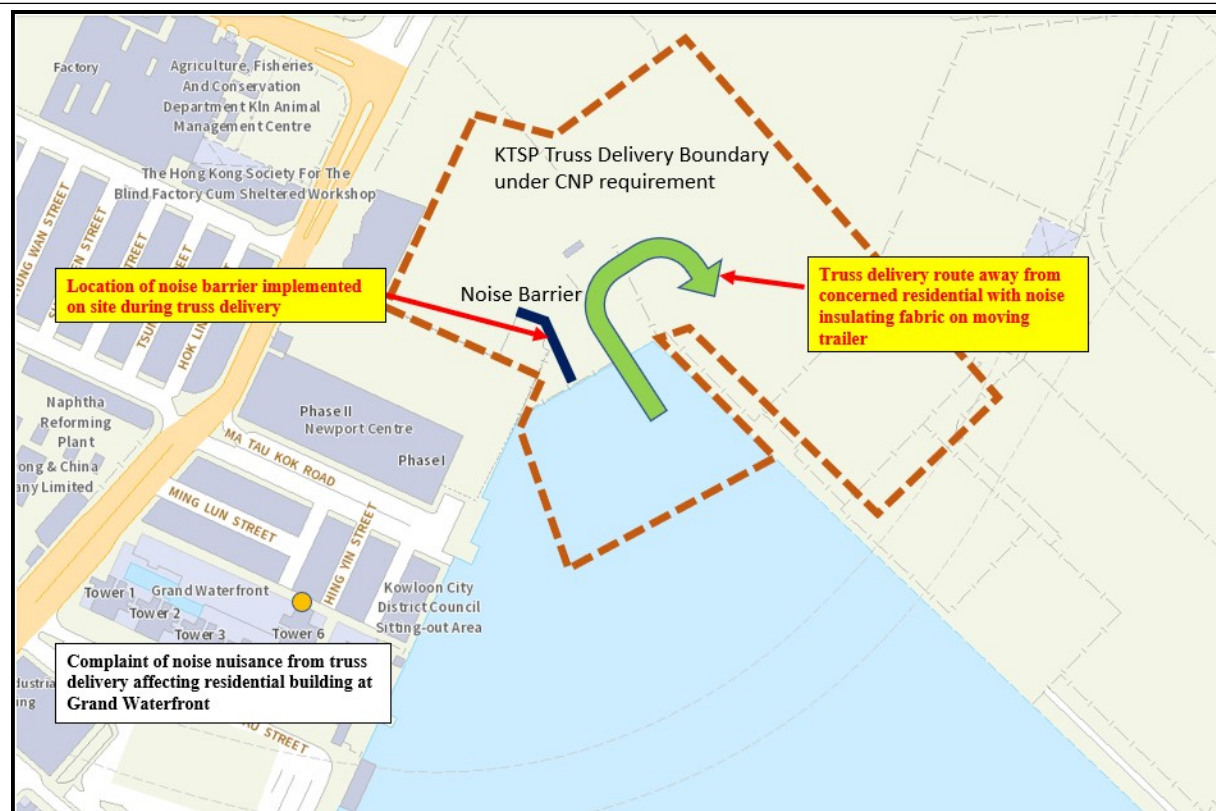

**Photo Records:**

**Environmental Measure Implemented:**



**Photos 1a and 1b:**

Noise barrier not less than 2m had been provided on site between the truss delivery working area and the Grand Waterfront according to the Construction Noise Permit (Ref. No. GW-RE0902-21) requirement. **(2 November 2021)**



Photos 2a and 2b:  
Noise insulating fabric implemented on moving trailer according to the CNP requirement.



Photo 3: The truss delivery works have been scheduled in the daytime as much as practicable to minimize the noise nuisance at nighttime. (3 November 2021)

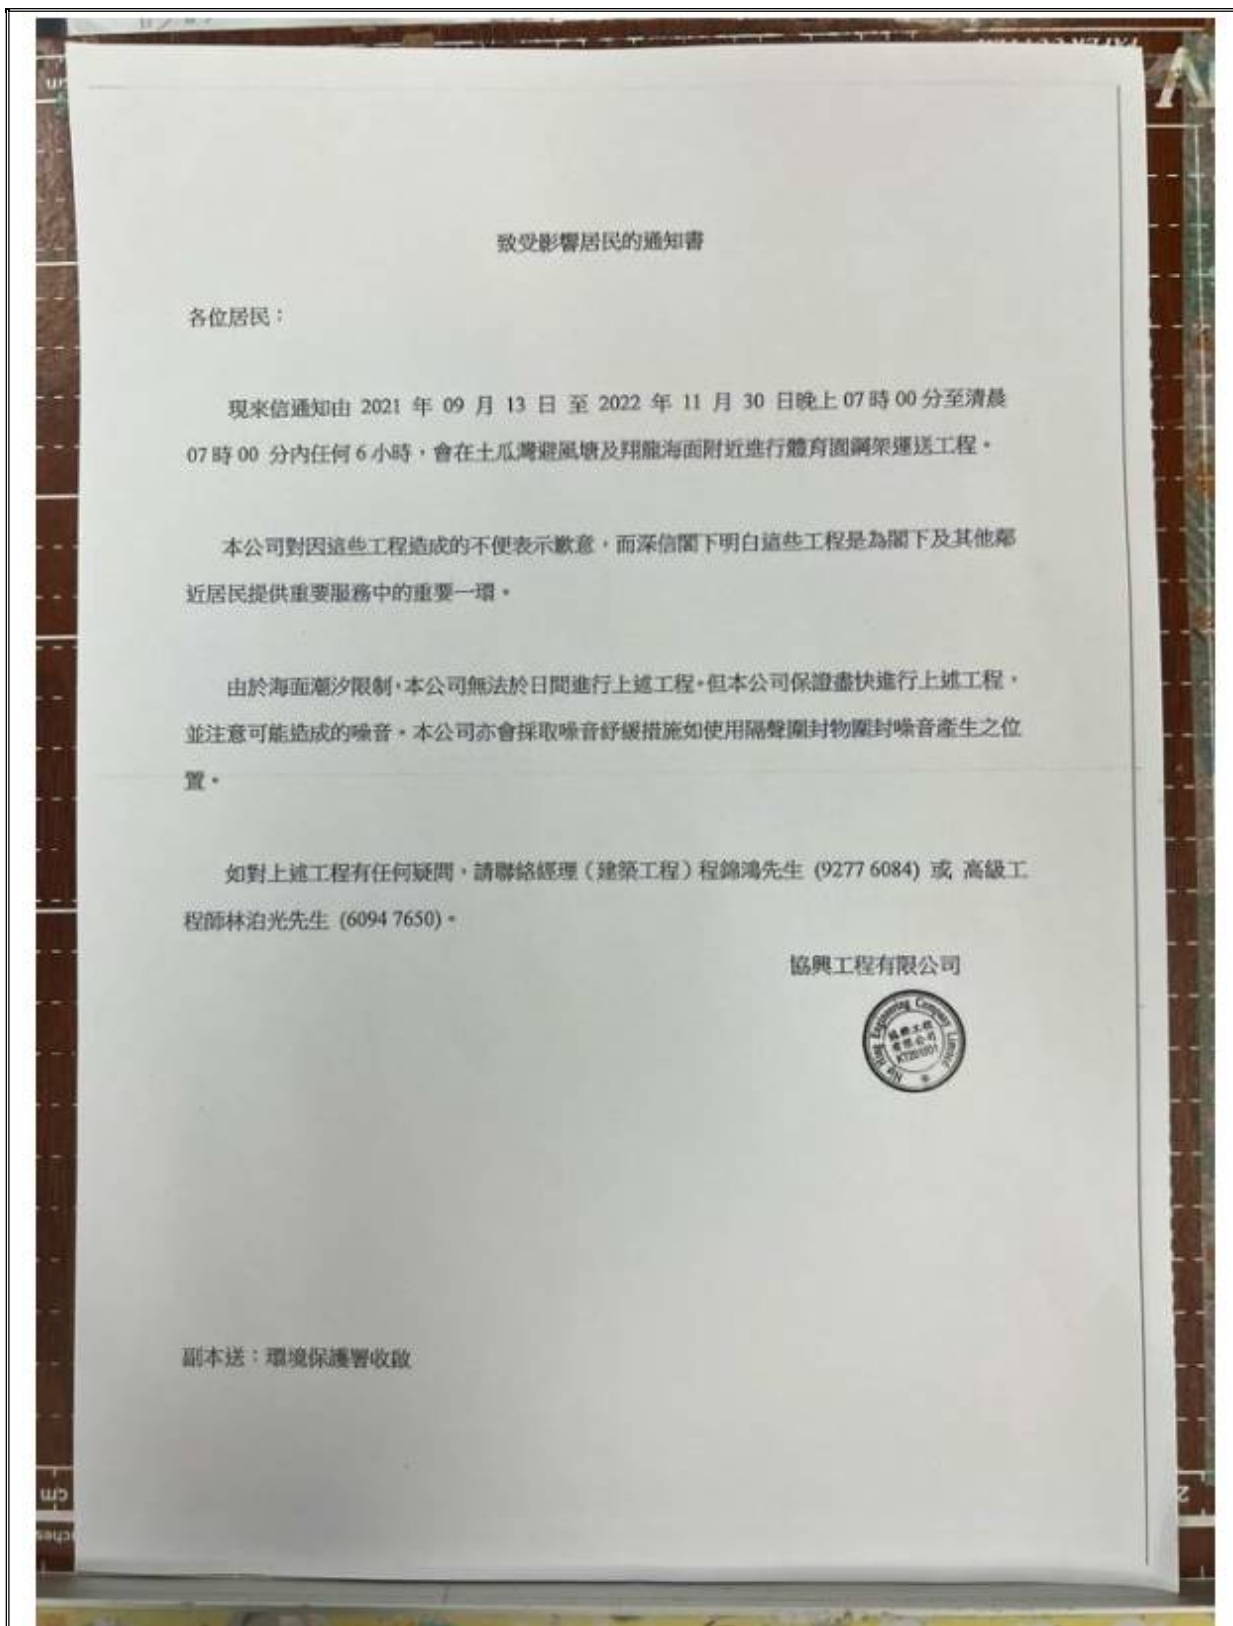


Photo 4: Advance notification of nighttime truss delivery work has been issued to nearby residential according to the CNP requirement.



Photo 5: Pre work briefing has been provided to ensure the compliance of CNP requirement to minimise potential noise nuisance during the nighttime truss delivery.

### Complaint Investigation Report

RECEIPT OF COMPLAINT		Ref: COM_0018
Date:	20 November 2021	
Time:	11:46	
From:	PS Chan (Hip Hing Construction Co., Ltd)	
Via:	Email	
Contact no.:	-	
COMPLAINANT		
Name:	-	Address: -
Contact no.:	-	
DETAILS OF COMPLAINT		
Date:	12 November 2021	
Time:	-	
Parameter:*	<del>Dust</del> Noise <del>Water</del> Other (specify):	
Description:	<p>- Complaint of noise nuisance arising from the truss delivery operation in late night on 12/11/2021.</p> <p>- Please ensure the works fulfill the relevant environmental legislation and conditions stipulated in the valid construction noise permit.</p> <p>- Please take necessary measures to minimize the environmental nuisance arising from the construction site.</p>	
INVESTIGATION RESULT & RESPONSE		
ET, IEC and SOR notified on:	20 and 22 November 2021	
Investigation conducted on:	23 November 2021	
Result of investigation:	<p>Complaint investigation was carried out on 23 November 2021, the results of investigation were summarized as following:</p> <p>According to the contractor's information, there was truss delivery work conducted on the complaint date (i.e. 12 November 2021.) There were nighttime truss delivery works carried out under the Construction Noise Permit (<b>Ref. No. GW-RE1090-21</b>) requirement:</p> <p><b>(i) 11 November 2021, 22:00– 23:59; and (ii) 12 November 2021, 00:00-04:00</b></p> <p>Noise mitigation control measures implemented on site included:</p> <ol style="list-style-type: none"> <li>Noise barrier not less than 2m had been provided on site between the truss delivery working area and the nearby residential area according to the CNP requirement. (photo 1)</li> <li>Noise insulating fabric implemented on moving trailer during nighttime truss delivery work. (photos 2a and 2b)</li> </ol> <p>In conclusion, noise control mitigation measures at the truss delivery port have been well implemented. All nighttime truss delivery operation works have fulfilled the relevant environmental legislation and CNP requirement during the concerned period. The contractor was reminded to maintain all necessary noise mitigation measures to minimise any potential noise nuisance to nearby residential during the nighttime truss delivery operation.</p>	



**RECOMMENDATIONS / MITIGATION MEASURES / ACTIONS**

Environmental mitigation measures have been maintained as follow:

1. The truss delivery works have been scheduled in the daytime as much as practicable to minimise the noise nuisance at nighttime. (photo 3)
2. Advance notification of nighttime truss delivery work has been issued to nearby residential according to the CNP requirement. (photo 4)
3. Pre work briefing has been provided to ensure the compliance of CNP requirement to minimise potential noise nuisance during the truss delivery. (photo 5)

Prepared by: Sunny Chan Title: Environmental Team Leader

Signature:  Date: 24 November 2021

**Attachment:**

- 1. Record of Construction Noise Permit - GW-RE1090-21**
- 2. Location Plan of the KTSP Truss Delivery Boundary**
- 3. Photo Records**

本署檔案  
OUR REF : (5) in EP631/K10/RE472960-21  
來函檔案  
YOUR REF :  
電話  
TEL NO : 2150 8002  
圖文傳真  
FAX NO : 2402 8275  
網址  
HOMEPAGE : <http://www.epd.gov.hk/>

Environmental Protection Department  
Environmental Compliance Division  
Regional Office (East)  
8/F., Cheung Sha Wan Government Offices,  
303 Cheung Sha Wan Road,  
Kowloon



環境保護署  
環保法規管理科  
區域辦事處(東)  
九龍長沙灣道303號  
長沙灣政府合署8樓

Registered Post

1 November 2021

To: HIP HING ENGINEERING COMPANY LIMITED  
11/F., Chevalier Commercial Centre,  
8 Wang Hoi Road,  
Kowloon Bay,  
Kowloon

Dear Sir,


**Advance notification to nearby residents in respect of works  
at Construction site of Kai Tak Sports Park (truss delivery port), Kai Tak, Kowloon  
under Construction Noise Permit No. GW-RE1090-21**

In connection with our Notice of Issue ref. (4) in EP631/K10/RE472960-21 dated 1 November 2021 of the captioned construction noise permit, please be advised that the permit was issued under a consideration of unavoidable constraints on working hours at the construction site concerned. Notwithstanding the noise control measures specified in the permit, the noise produced by the works is expected to exceed the statutory noise limit, thus causing disturbance to the nearby residents. This may result in noise complaints which may affect the image of your company.

As a measure to alert the affected persons, and to help maintain good public relations and reduce noise complaints, you are strongly advised to notify the nearby residents by providing details such as dates and hours of operation, location and nature of works, and contact telephone numbers to them a few days in advance of the construction. A sample notice to be posted to residential building notice boards is attached for your use. Please also send a copy of the notice to the undersigned by facsimile for our information a few days prior to the commencement of the construction.

Your cooperation in this matter is highly appreciated.

Yours faithfully,

  
(WONG Chor-kuen, Alfred)  
Senior Environmental Protection Officer  
for Director of Environmental Protection

c.c. Home Affairs Bureau  
[Attn: Mr. XU Wei Hao (E(RS))]  
(Fax no. 3586 0591)

(5) in EP631/K10/RE472960-21

2150 8002

2402 8275

掛號函件

致： 九龍 九龍灣  
宏開道 8 號  
其士商業中心 11 樓  
協興工程有限公司

執事先生：

根據「建築噪音許可證第 GW-RE1090-21 號」  
於九龍啟德啟德體育園的建築地盤(桁架卸貨港)進行工程前預先知會附近居民

本辦事處在二零二一年十一月一日發信(檔號(4) in EP631/K10/RE472960-21)通知你，上述「建築噪音許可證」已經發出，就此再函說明，我們是鑑於貴方在有關工地的施工時間難免受限制，因而簽發該許可證。儘管許可證上已列各項噪音控制措施，但工程產生的噪音，預計仍會超出法定噪音規限，滋擾鄰近住戶，或有可能引起噪音滋擾投訴，影響貴公司的形象。

為方便受影響的人士察覺有關的情況，並保持良好的公共關係，減少噪音滋擾投訴，本處籲請你在施工前數天知會鄰戶，說明工程的詳情，例如進行工程的日期和時間、工程的地點和性質，以及查詢的電話號碼。隨函夾附可供在住宅大廈告示板上張貼的告示式樣，以供參考。此外，請在進行工程前數天，以傳真方式交來告示副本備閱。

多謝合作。

環境保護署署長

(王楚權



代行)

副本送： 民政事務局  
[經辦人：徐維浩 先生(工程師(康樂及體育))]  
(傳真號碼：3586 0591)

二零二一年十一月一日

Notice to Affected Residents  
(SAMPLE)

(DATE)

Dear Residents,

I am writing to let you know that we will be carrying out \_\_\_\_\_  
\_\_\_\_\_ in the vicinity of  
(Nature of works : e.g. drainage maintenance works)  
\_\_\_\_\_ during the  
(Location : e.g. XYZ Street between ABC Road and DEY Road)  
hours of \_\_\_\_\_ from \_\_\_\_\_ to \_\_\_\_\_.  
(e.g. 10:00 pm to 1:00 am) (Period : e.g. 15 January 2015 to 18 January 2015)

I wish to apologize for the inconvenience that this may cause you while I am sure you will understand that such works are an integral part of providing essential services to you and other residents in your neighbourhood.

You may like to note that it is not possible for us to conduct the works during the day time hours due to \_\_\_\_\_.  
(Reasons : e.g. traffic conditions)

Please be assured that we will carry out the works as quickly as possible with due regard to the noise intrusion which may result. We will also be adopting noise mitigation measures such as \_\_\_\_\_.  
(e.g. low noise generator enclosed by an acoustical enclosure)

If you have any enquiries regarding the works, please feel free to contact our \_\_\_\_\_  
(Representative : e.g. works supervisor, Mr. A.B. Cee at Mobile Phone or Pager No. or Mr. E.F. Gee, engineer at Phone : xxxx-yyyy)

Yours truly,

(NAME)

(POST)

(NAME OF COMPANY)

致受影響居民的通知書

(樣本)

各位居民：

現來信通知由\_\_\_\_年\_\_月\_\_日至\_\_\_\_年\_\_月\_\_日\_\_\_\_時至\_\_\_\_時在  
(時期：例如 2015 年 1 月 15 日至 2015 年 1 月 18 日 (例如晚上 10 時至零晨 1 時))

\_\_\_\_\_  
(位置：例如 ABC 道與 DEF 道之間的 XYZ 街)

附近進行\_\_\_\_\_。  
(工作性質：例如 排水渠維修工程)

本公司對因這些工程造成的不便表示歉意，而深信閣下明白這些工程是為閣下及其他鄰近居民提供重要服務中的重要一環。

在日間由於\_\_\_\_\_，本公司無法進行上述工程，  
(理由：例如交通情況)

但本公司保證盡快進行上述工程，並注意可能造成的噪音。本公司亦會採取噪音紓緩措施如\_\_\_\_\_。  
(例如由隔聲圍封物圍封低噪音產生器)

如對上述工程有任何疑問，請聯絡\_\_\_\_\_ [代表：例如工程主管，ABC 先生 (手提

\_\_\_\_\_。  
電話號碼或傳呼號碼) 或工程師 EFG 先生，電話號碼，xxxx-yyyy]

\_\_\_\_\_  
公司名稱

\_\_\_\_\_  
職位

\_\_\_\_\_  
姓名

副本送：環境保護署 (CI(RE)5 - 傳真號碼：2756 8588)

本署檔案  
OUR REF : (4) in EP631/K10/RE472960-21  
來函檔案  
YOUR REF :  
電話  
TEL NO : 2150 8002  
圖文傳真  
FAX NO : 2402 8275  
網址  
HOMEPAGE : <http://www.epd.gov.hk/>

Environmental Protection Department  
Environmental Compliance Division  
Regional Office (East)  
8/F., Cheung Sha Wan Government Offices,  
303 Cheung Sha Wan Road,  
Kowloon



環境保護署  
環保法規管理科  
區域辦事處(東)  
九龍長沙灣道303號  
長沙灣政府合署8樓

Registered Post

1 November 2021

To: HIP HING ENGINEERING COMPANY LIMITED  
11/F., Chevalier Commercial Centre,  
8 Wang Hoi Road,  
Kowloon Bay,  
Kowloon

Dear Sir,

**Notice of Issue of Construction Noise Permit pursuant  
to section 8(6) of the Noise Control Ordinance (Cap. 400)**

I write to inform you that, under section 8(6) of the Noise Control Ordinance, the Authority has decided to issue a construction noise permit in respect of your application, which was received by the Authority on 22 October 2021, **for the use of powered mechanical equipment for carrying out construction work at Construction site of Kai Tak Sports Park (truss delivery port), Kai Tak, Kowloon.**

The construction noise permit No. GW-RE1090-21 is enclosed.

Please note that a condition concerning **online submission of advance notification of work** to the Authority has been incorporated into this construction noise permit. You are strongly advised to read the conditions of the permit carefully and to ensure compliance with these conditions. Any breaching of the conditions may lead to cancellation of the permit, **subsequent prosecution action** and/or the Authority's refusal to issue further permit for the above construction site.

Yours faithfully,

  
(WONG Chor-kuen, Alfred)  
for Authority

Note:

Electronic submission of application for construction noise permit is available at Environmental Protection Department's website. File attachments with total size not exceeding 20 MB in acceptable format are allowed for electronic submission. Electronic application form can be downloaded from our website (<https://epic.epd.gov.hk/eForm/ChangeLanguage.do?language=eng&url=/pages/datadownload/downloadMain.jsp>) and an overview of application submission (<https://epic.epd.gov.hk/eForm/introduce.html>) is provided for more information.

(4) in EP631/K10/RE472960-21

2150 8002

2402 8275

掛號函件

致： 九龍 九龍灣  
宏開道 8 號  
其士商業中心 11 樓  
協興工程有限公司

執事先生：

**根據《噪音管制條例(第 400 章)》第 8(6)條  
發出的通知書 — 簽發「建築噪音許可證」**

本監督於二零二一年十月二十二日，收到你擬於下述地址：九龍啟德啟德體育園的建築地盤(桁架卸貨港)，使用機動設備進行建築工程而提出的「建築噪音許可證」申請，現根據《噪音管制條例》第 8(6)條的規定通知你，上述的申請已被批准。

隨函附上「第 GW-RE1090-21 號建築噪音許可證」。

請注意，有關施工前於網上預先通知本監督的要求已納入本建築噪音許可證的條件。請細閱及確保遵守許可證各項條件。如有違反，本監督可撤銷許可證、提出檢控及/或拒絕再就上述地盤簽發任何「建築噪音許可證」。

監 督

(王楚權



代行)

二零二一年十一月一日

注意：

環境保護署提供網上申請「建築噪音許可證」服務。網上申請容許上傳檔案總容量不大於 20 MB 的有關文件。可於本署網頁下載電子表格  
(<https://epic.epd.gov.hk/eForm/ChangeLanguage.do?language=eng&url=/pages/datadownload/downloadMain.jsp>)  
及參閱電子表格提交服務概覽(<https://epic.epd.gov.hk/eForm/introduce.html>)，了解更多資料。

FORM 3  
NOISE CONTROL ORDINANCE  
(Chapter 400)  
SECTION 8(9)

[reg.5(a)]

**CONSTRUCTION NOISE PERMIT FOR THE USE OF POWERED  
MECHANICAL EQUIPMENT FOR THE PURPOSE OF CARRYING OUT  
CONSTRUCTION WORK OTHER THAN PERCUSSIVE PILING AND/OR  
THE CARRYING OUT OF PRESCRIBED CONSTRUCTION WORK**

CONSTRUCTION NOISE PERMIT NO. GW-RE1090-21

To : HIP HING ENGINEERING COMPANY LIMITED

This construction noise permit is issued in accordance with section 8 of the Noise Control Ordinance. Permission is granted for the use of powered mechanical equipment for the purpose of carrying out construction work other than percussive piling and/or the carrying out of prescribed construction work, subject to the conditions set out below. The carrying out of construction work otherwise than in accordance with the conditions may result in the permit being cancelled and in a prosecution for an offence.

*CONDITIONS*

1. Construction site where the powered mechanical equipment and/or prescribed construction work may be employed:

Full address: Construction site of Kai Tak Sports Park (truss delivery port), Kai Tak, Kowloon.

Lot No.: ---

The site boundary, that is, the boundary of the area within which the powered mechanical equipment may be used and the prescribed construction work may be carried out is delineated on the attached plan which forms part of this construction noise permit.

2. \* PART/WHOLE of the site falls \* WITHIN/OUTSIDE a designated area.

3. Powered Mechanical Equipment

- a. Items of powered mechanical equipment which may be used inside the site boundary :

<i>Identification code of item of powered mechanical equipment (if applicable)</i>	<i>Description of item of powered mechanical equipment</i>	<i>No. of units</i>
<b>Group A</b>	Self-propelled trailer	Six
---	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level $\leq 94$ dB(A)	One
<b>Group B</b>	Crane, mobile (diesel)	One
CNP 048	Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level $\leq 94$ dB(A)	One
---	Flat top barge	One
CNP 221	Tug boat	One

- b. Validity of the construction noise permit for the use of the powered mechanical equipment:

Date and time of commencement : 3 November 2021 at 1900 hours

Days and hours : 0000-2400 hours on general holidays (including Sundays), 0000-0700 hours and 1900-2400 hours on any day not being a general holiday.

This part of the permit expires on : 2 February 2022 at 2400 hours

- c. One photograph, endorsed by the Authority, of each item of powered mechanical equipment described in this construction noise permit is required to be kept on the construction site and made available for inspection by the Authority.

- d. Other conditions imposed on the use of the powered mechanical equipment:

Please refer to attached sheet for conditions imposed for this construction noise permit which is issued as a special case due to constraints on working hours governed by tidal conditions.



4. Prescribed Construction Work

a. Type of prescribed construction work which may be carried out inside the site boundary:

<i>Identification code of type of prescribed construction work</i>	<i>Description of type of prescribed construction work</i>
	Not applicable

b. Validity of the construction noise permit for the carrying out of the prescribed construction work:

Date and time of commencement : ..... Not applicable ..... at ..... Not applicable .....  
 Date and hours : .. Not applicable ..

This part of the permit expires on : ..... Not applicable ..... at : ..... Not applicable .....

c. ~~Site layout plan(s), endorsed by the Authority, may be attached with the permit to indicate the locations permitted for the carrying out of prescribed construction work described in this permit. The layout plan(s) is(are) required to be kept on the construction site and made available for inspection by the Authority.~~

d. Other conditions imposed on the carrying out of the prescribed construction work:

.....  
 .....  
 .....

5. This construction noise permit or a copy thereof must be displayed on the construction site at all vehicular entrances for public information.

.....  
 .....

Dated this 1<sup>st</sup> day of November 2021

Signed : .....  
 (WONG Chor-kuen, Alfred)  
 for Authority

\* Delete as necessary

表格 3  
 噪音管制條例  
 (第400章)  
 第8(9)條

建築噪音許可證  
 為進行建築工程（撞擊式打樁除外）  
 而使用機動設備及／或進行訂明建築工程

建築噪音許可證編號：..... GW-RE1090-21 .....

致：...協興工程有限公司.....

本建築噪音許可證是按照《噪音管制條例》第8條的規定而發出的。現准予使用機動設備以進行撞擊式打樁工程以外的建築工程及／或進行訂明建築工程，但須受以下條件規限。若不按照該等條件進行建築工程，許可證可遭撤銷，而且會受到檢控。

條 件

1. 可使用機動設備及／或進行訂明建築工程的建築地盤：

詳細地址：九龍啟德啟德體育園的建築地盤(桁架卸貨港).....

地段編號：.....

地盤範圍(即可使用機動設備及進行訂明建築工程的地方範圍)已描劃於夾附的圖則上，而該圖則是本建築噪音許可證的一部分。

2. 該地盤部分／全部\*位於指定範圍之內／外\*。

3. 機動設備

- a. 在地盤範圍內可使用的各項機動設備：

各項機動設備的識辨代碼 (如適用的話)	各項機動設備的說明	數目
<b>A組</b> ---	自行車拖車	陸
---	發電機，備有優質機動設備標籤顯示聲功率級≤94分貝(A)	壹
<b>B組</b> CNP 048	起重機，流動(油渣)	壹
---	發電機，備有優質機動設備標籤顯示聲功率級≤94分貝(A)	壹
---	平頂躉船	壹
CNP 221	拖船	壹

- b. 可使用機動設備的建築噪音許可證有效期：

生效日期及時間：..... 二零二一年十一月三日..... 下午七時.....

日期及時間：...公眾假日(包括星期日)的凌晨零時至晚上十二時，公眾假日以外的任何一日凌晨零時至上午七時及下午七時至晚上十二時。.....

此部分許可證屆滿日期及時間：..... 二零二二年二月二日..... 晚上十二時.....

日期 時間

- c. 建築地盤須備有本建築噪音許可證所述每件機動設備的照片各一幀，供監督隨時查看；該等照片須經監督認可。

- d. 規限使用機動設備的其他條件：

請參見附頁有關本建築噪音許可證的規限條件。該條件是鑒於本建築噪音許可證屬特別個案而註明的，而該特別個案是施工時段受潮汐限制。.....

4. 訂明建築工程

a. 在地盤範圍內可進行的訂明建築工程：

訂明建築工程的識辨代碼	訂明建築工程的類別的說明
	不適用

b. 可進行訂明建築工程的建築噪音許可證有效期期：

生效日期及時間：不適用

日期及時間：不適用。

此部分許可證屆滿日期及時間：不適用

c. 本許可證可夾附經監督認可的地盤圖則，以顯示本許可證准予進行訂明建築工程的點。該地盤圖則須存放於建築地盤供監督隨時查看。

d. 規限進行訂明建築工程的其他條件：

5. 本建築噪音許可證或其副本必須展示於建築地盤的所有車輛入口處，給予公眾人士參閱。

日期：2021 年 11 月 1 日



簽署：\_\_\_\_\_

監督  
(王楚權 代行)

\* 刪去不適用者

SPECIAL CASE -due to constraints on  
working hours governed by tidal conditions  
特別個案 - 施工時段受潮汐限制

Page 1 of 1

**Sheet attached to Construction Noise Permit  
No. GW-RE1090-21**

3.d. Other conditions imposed on the use of the powered mechanical equipment:

1. The powered mechanical equipment shall not be used more than **20 days** during the validity period of this Construction Noise Permit.
2. All care shall be taken to ensure that the construction work is carried out as quickly as possible with due regard for the potential noise intrusion which may result.
3. Only one group of the powered mechanical equipment listed in condition 3.a shall be allowed to operate at any time.
4. The mobile crane (diesel) (CNP 048) shall be operated at the location as marked on the attached plan.
5. The power generating part of Self-propelled trailer shall be enclosed by a canvas acoustic shroud of vinyl sheets or equivalent.
6. Noise barrier with minimum 2 metres high shall be installed at the location as marked on the attached plan.
7. The powered mechanical equipment covered by this Construction Noise Permit shall not be operated when any powered mechanical equipment covered by the Construction Noise Permit No. GW-RE0833-21 is being operated.
8. All flaps and panels of the generator shall be closed during operation.
9. All idling powered mechanical equipment shall be switched off.
10. Portable phones or walkie-talkies with headphones shall be used for site communication. No whistles, horns and loudspeakers shall be used. No shouting shall be allowed.
11. The construction work in relation to this Construction Noise Permit shall only be carried out with prior notification to the Authority of the location, date and time of the work as well as the details of work program (including the date and time for carrying out different phases or sequence of work ) etc. Such notification shall be made by logging in the following webpage (<http://cnp-advancenotification.hk>) and submitting all information required. Such notification shall be made within 14 days but no less than 48 hours before commencement of work for every work location.

Signed : \_\_\_\_\_

(WONG Chor-kuen, Alfred)  
for Authority

建築噪音許可證  
編號 GW-RE1090-21 的附頁

3. d. 規限使用機動設備的其他條件：


1. 祇可在此建築噪音許可證的有效期內使用機動設備不超過二十天。
2. 本許可證持有人必須確保竭力從速完成該等建築工程，並小心防範會引起的噪音干擾。
3. 在任何時間內，祇可使用列在條件 3. a 內的其中一組機動設備。
4. 流動起重機(油渣) (CNP 048)必須在附圖上標示的位置操作。
5. 自行式拖車的動力產生部份必須用合成隔音屏障或同等物料圍封。
6. 必須在附圖上標示的位置上裝設高度不低於 2 米的隔音屏障。
7. 當建築噪音許可證編號 GW-RE0833-21 內的任何機動設備正在操作時，不可操作本建築噪音許可證內的機動設備。
8. 發電機的所有覆蓋及嵌板於操作時必須關閉。
9. 關掉所有空轉的機動設備。
10. 地盤通訊必須使用手提電話或連耳筒對講機，不准使用哨子、號角及擴音器，不准喧嘩。
11. 在進行此建築噪音許可證內所載列的建築工程時，必須確保就每個施工地點於施工前 48 小時至施工前 14 日內，登入以下網上平台 (<http://cnp-advancenotification.hk/tc>) 並就每個施工地點於施工前 48 小時至施工前 14 日內填妥及提交有關施工地點、日期及時間、及施工程序安排(包括不同階段或工序施工日期及時間的安排)等所需資料。



簽署：\_\_\_\_\_

監督  
(王楚權 代行)

Photograph(s) attached to Construction Noise Permit No. GW-RE1090-21  
建築噪音許可證編號：GW-RE1090-21 的照片

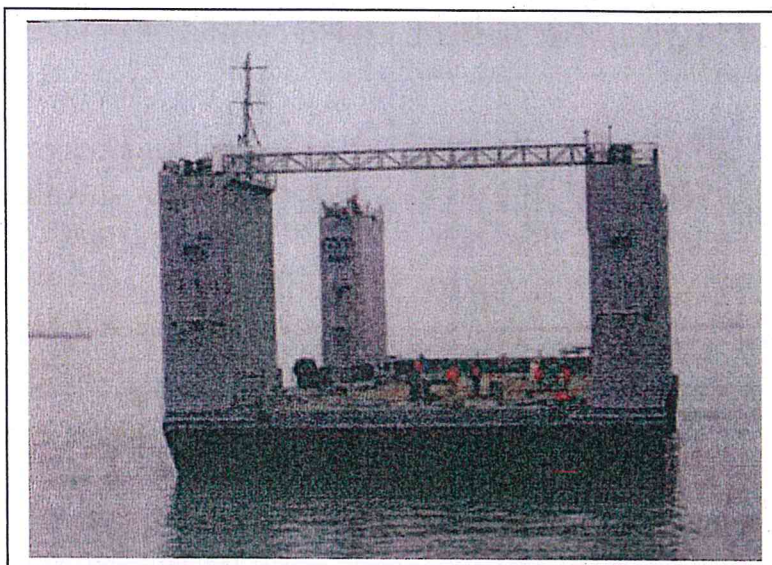

Flat top barge  
平頂躉船



CNP 221 Tug boat  
拖船



Photograph(s) attached to Construction Noise Permit No. GW-RE1090-21  
建築噪音許可證編號：GW-RE1090-21 的照片




Self-propelled trailer  
自行式拖車




CNP 048 Crane, mobile (diesel)  
起重機，流動 (油渣)



**Photograph(s) attached to Construction Noise Permit No. GW-RE1090-21**  
**建築噪音許可證編號：GW-RE1090-21 的照片**

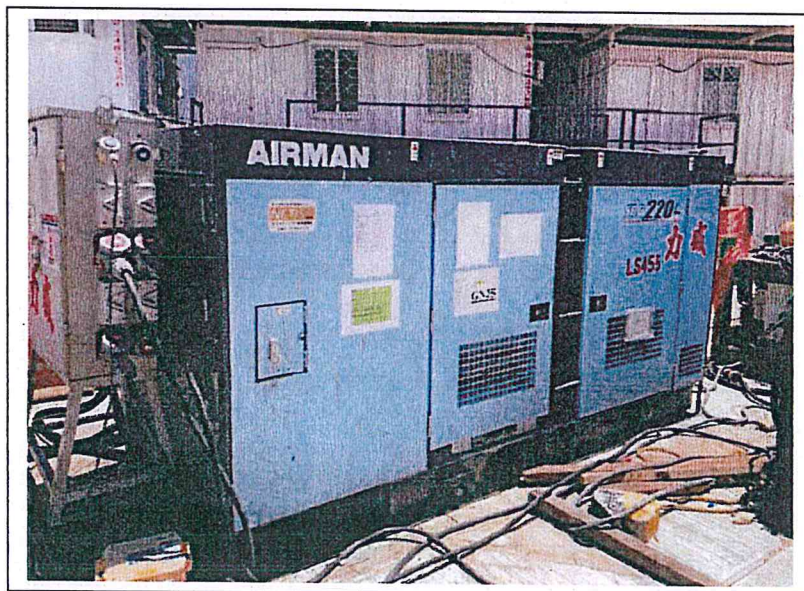

Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level  $\leq 94$  dB(A)  
發電機，備有優質機動設備標籤顯示聲功率級  $\leq 94$  分貝(A)

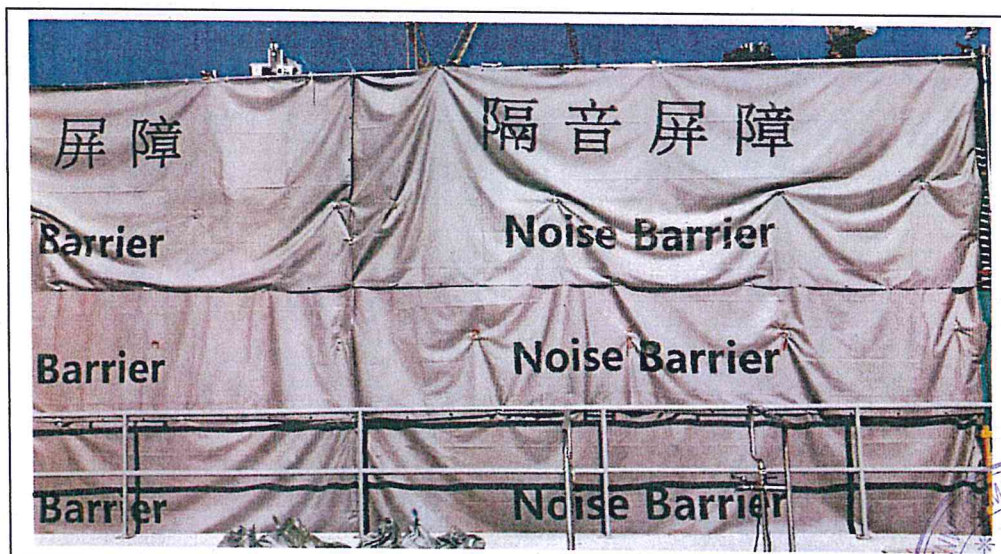


Noise barrier  
隔音屏障







Location of Construction Site 建築地盤的位置		
Location	Northing	Easting
A	820561	838420
B	820312	838510
C	820125	838350
D	820202	838264
E	820196	838242
F	820142	838295
G	820082	838192
H	820149	838162
I	820176	838175
J	820216	838085
K	820291	838119
L	820278	838168
M	820346	838245
N	820474	838257
O	820492	838235
P	820513	838258

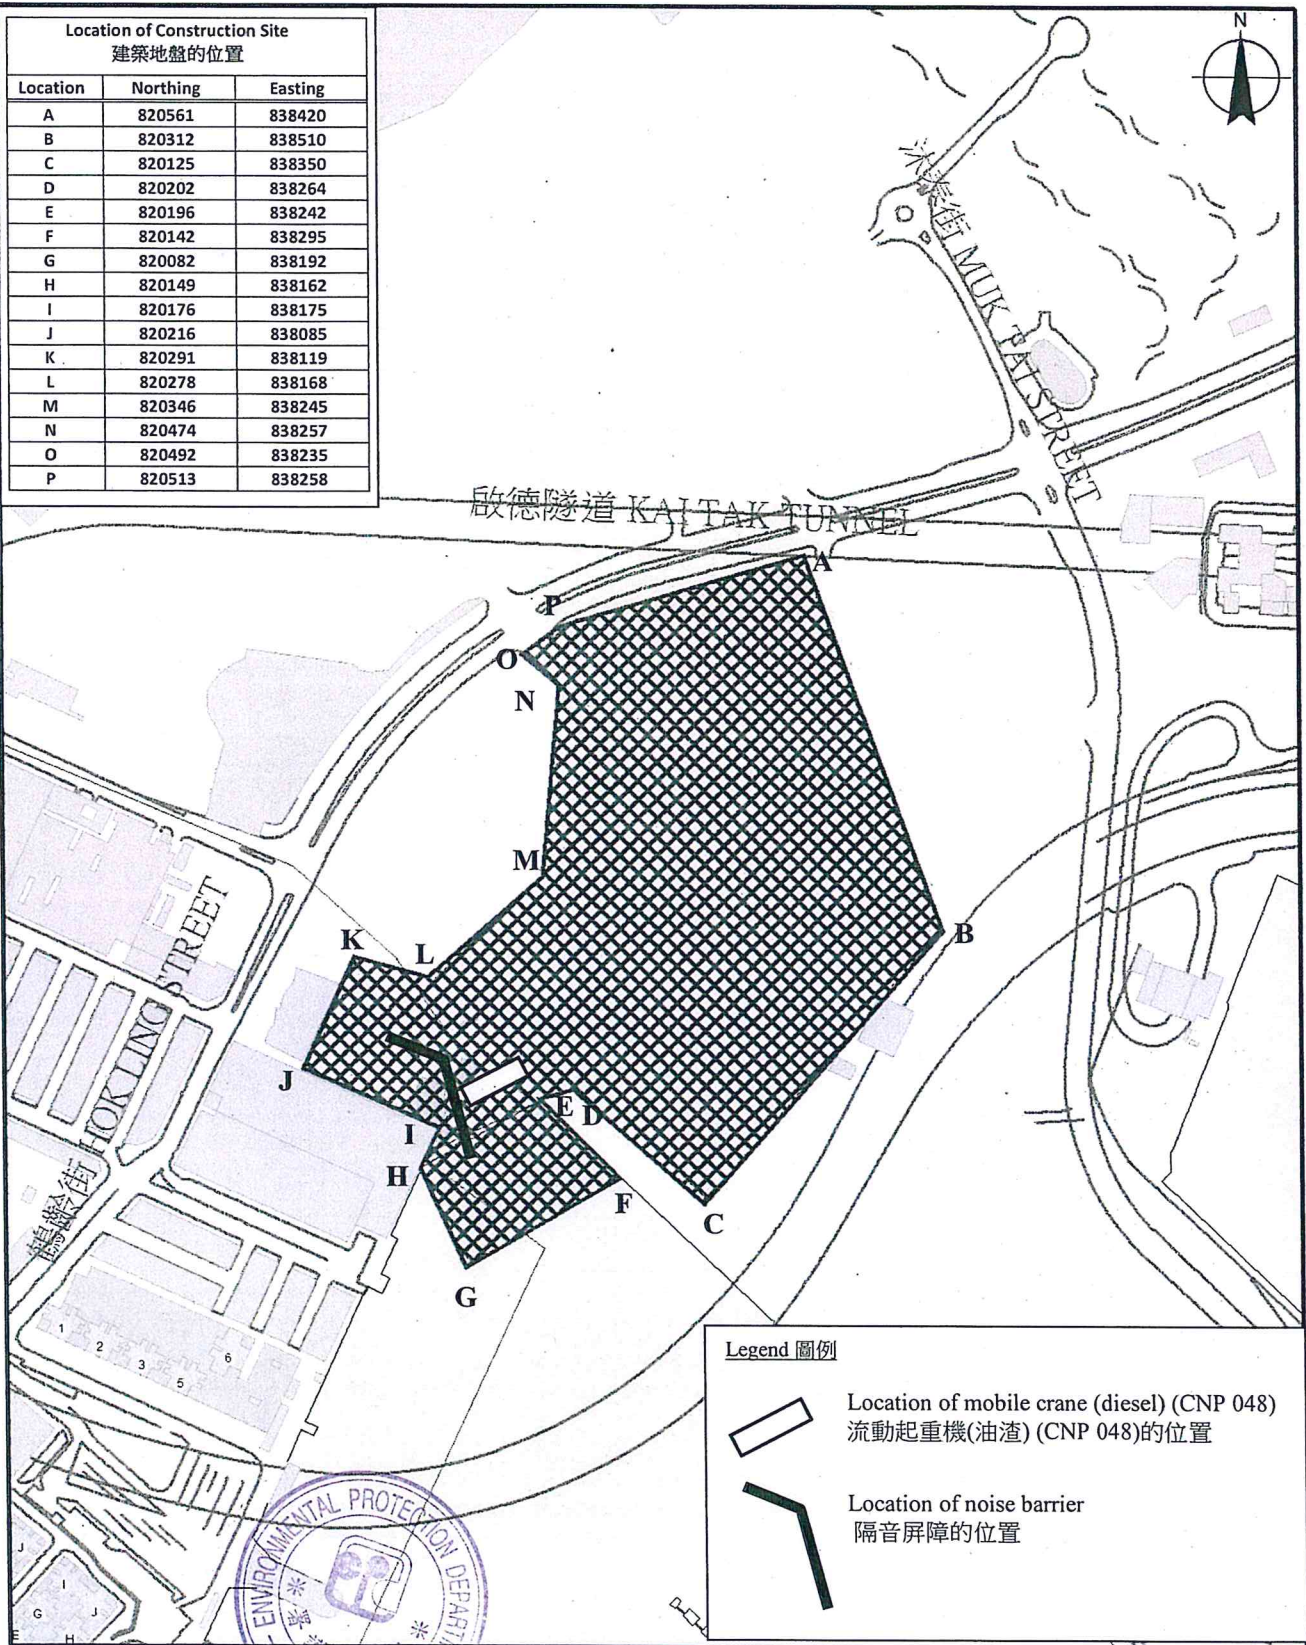


環境保護署  
Environmental Protection Department  
Noise Control Authority  
噪音管制監督

圖例 Legend  
 建築地盤 Construction Site

建築噪音許可證編號 GW-RE1090-21 的附圖  
Plan attached to Construction Noise Permit No. GW-RE1090-21

比例 Scale 1:5,000  
 米 Meters  
0 25 50 100 150

### Location Plan of the KTSP Truss Delivery Boundary

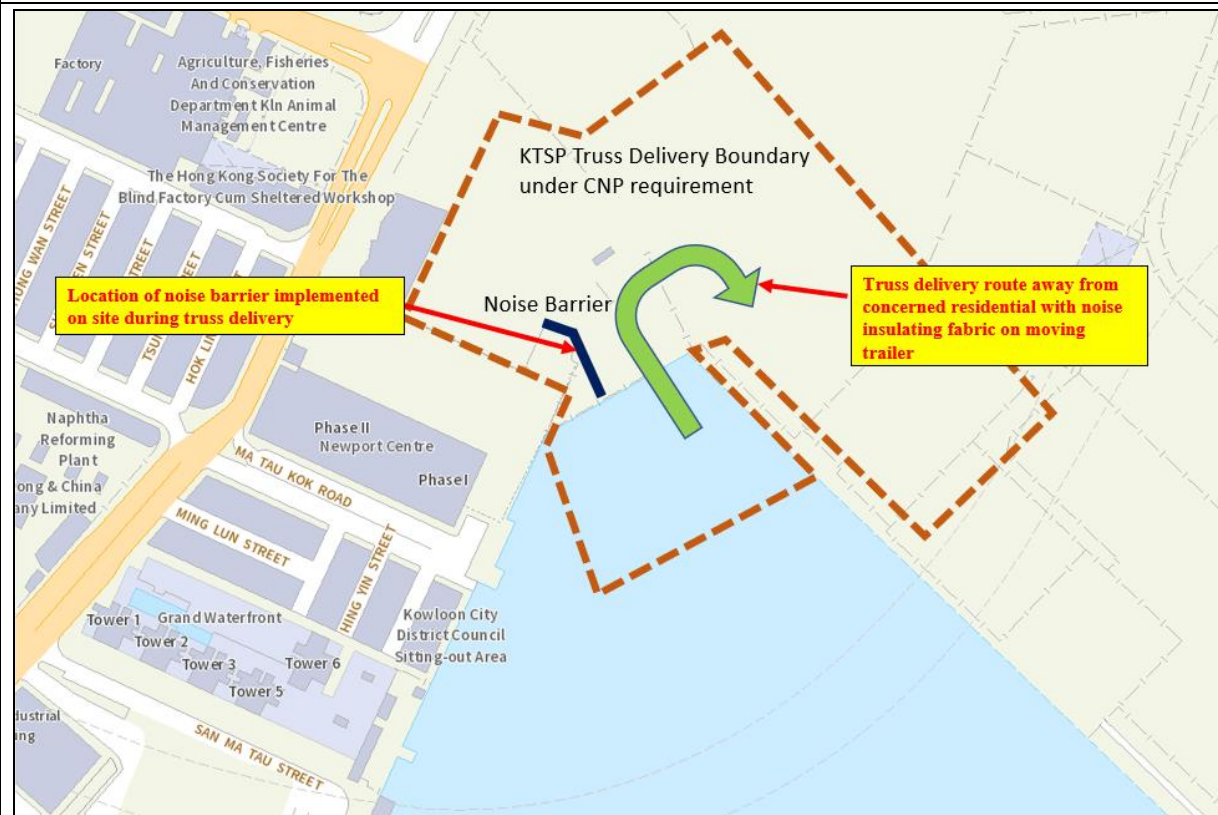

**Photo Records:**

**Environmental Measure Implemented:**



Photos 1:

Noise barrier not less than 2m had been provided on site between the truss delivery working area and the nearby residential area according to the Construction Noise Permit (Ref. No. GW-RE1090-21) requirement. **(23 November 2021)**



Photos 2a and 2b:  
Noise insulating fabric implemented on moving trailer according to the CNP requirement.  
(12 November 2021)

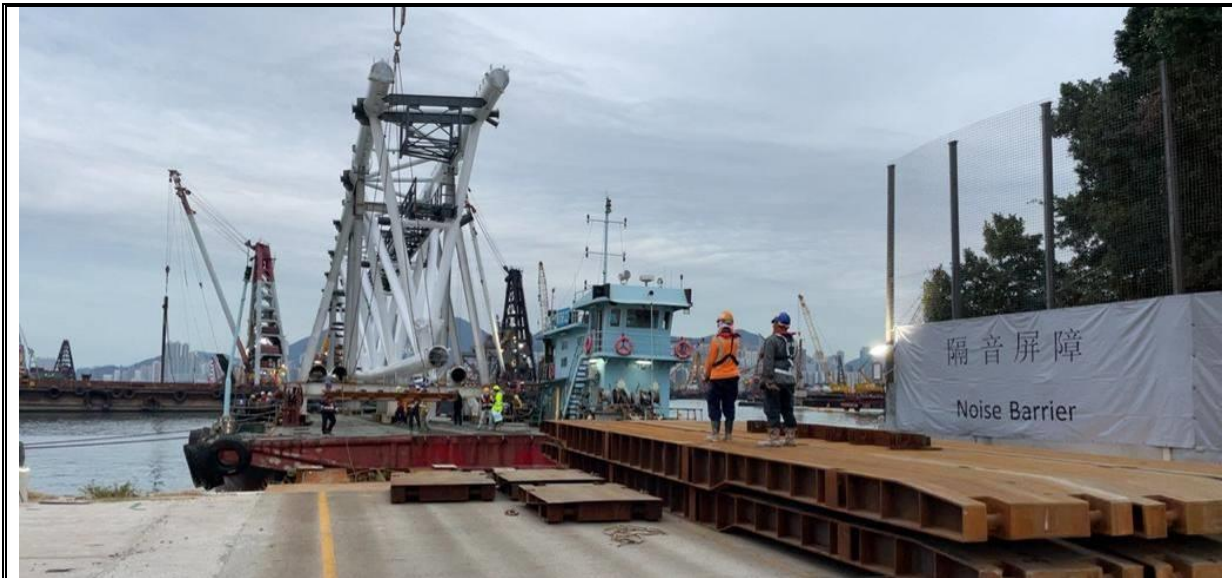


Photo 3: The truss delivery works have been scheduled in the daytime as much as practicable to minimize the noise nuisance at nighttime. (22 November 2021)

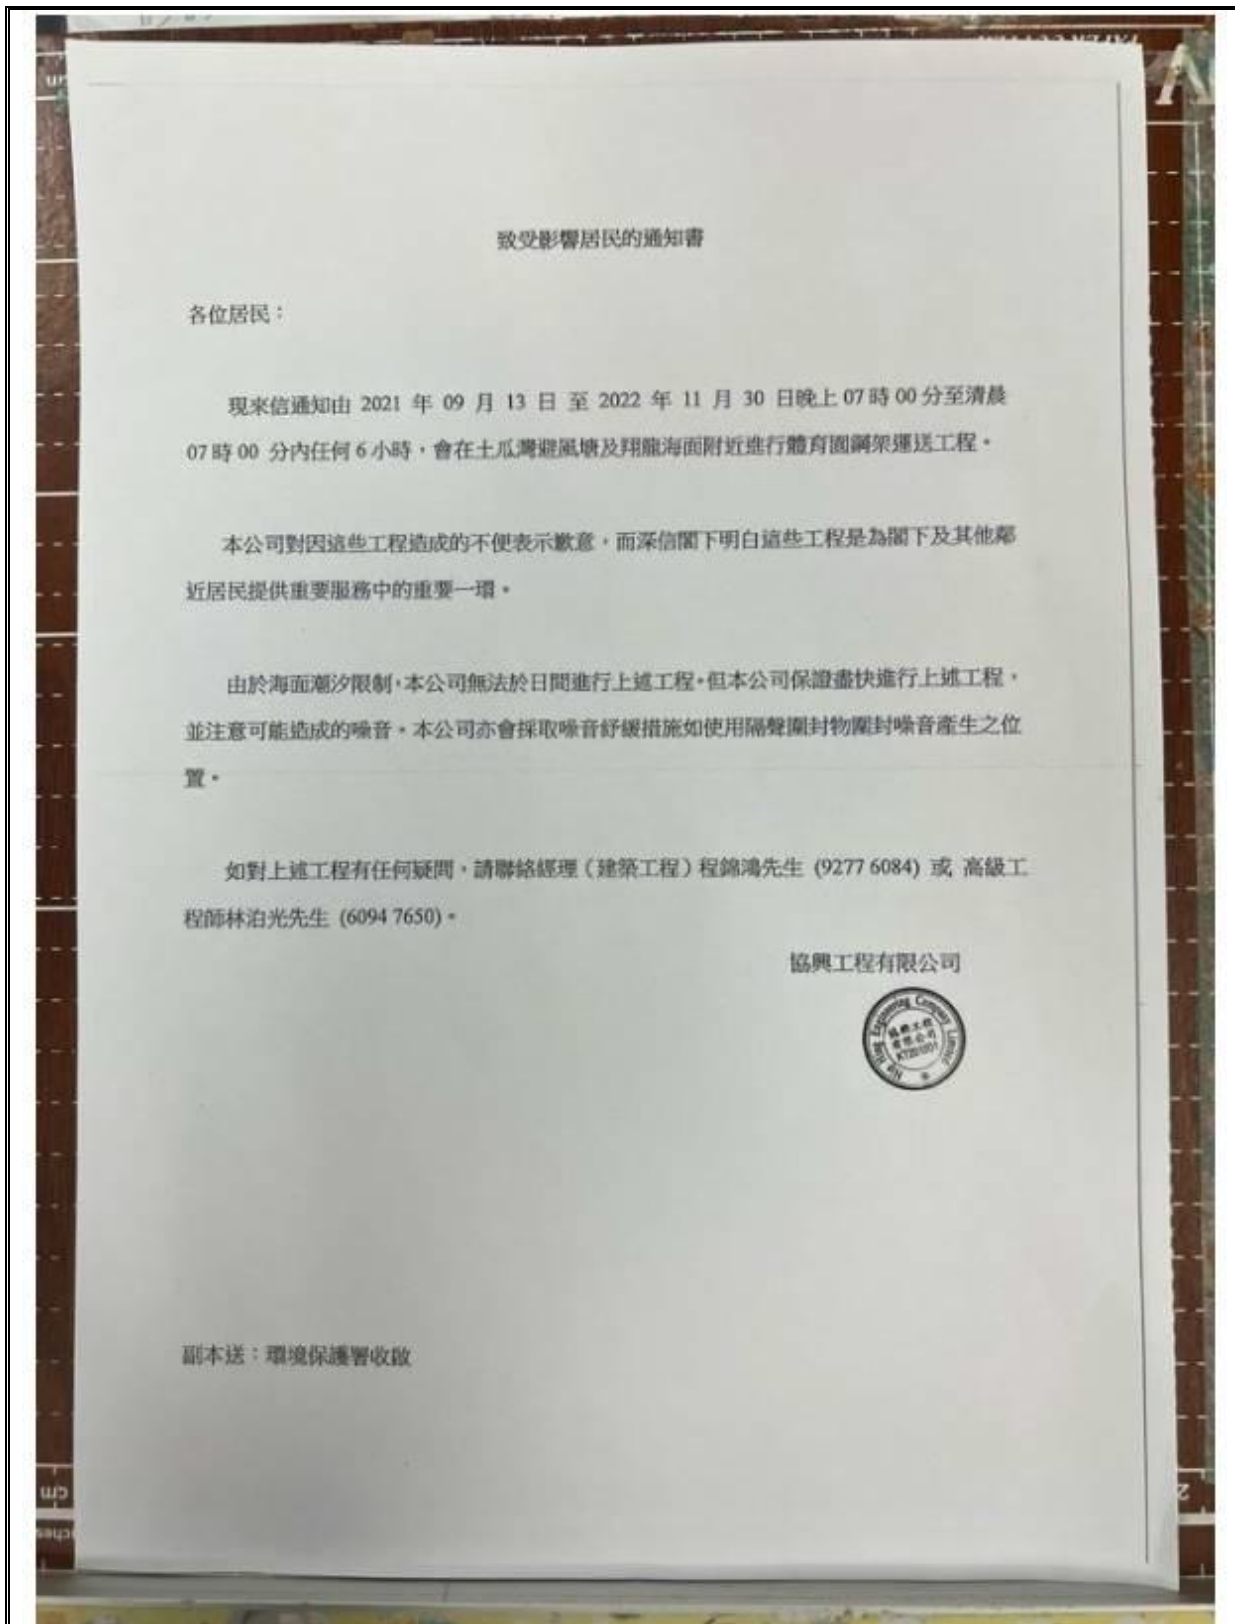


Photo 4: Advance notification of nighttime truss delivery work has been issued to nearby residential according to the CNP requirement.



Photo 5: Pre work briefing has been provided to ensure the compliance of CNP requirement to minimise potential noise nuisance during the nighttime truss delivery.  
**(11 November 2021)**
