

# Hong Kong Kwong Tai Builders Limited


Contract No. SSW 317

## Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point

Environmental Monitoring and Audit Monthly Report

June 2010

(Version 1.2)

Certified By	 _____ Dr. Priscilla Choy (Environmental Team Leader)
--------------	--

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

### CINOTECH CONSULTANTS LTD

Room 1710, Technology Park,

18 On Lai Street,

Shatin, NT, Hong Kong

Tel: (852) 2151 2083 Fax: (852) 31071388

Email: [info@cinotech.com.hk](mailto:info@cinotech.com.hk)

## TABLE OF CONTENTS

	<b>Page</b>
<b>EXECUTIVE SUMMARY .....</b>	<b>1</b>
<b>1 INTRODUCTION.....</b>	<b>4</b>
Background .....	4
Project Organizations .....	5
Construction Programme.....	5
Summary of EM&A Requirements.....	6
<b>2 NOISE .....</b>	<b>7</b>
Monitoring Requirements .....	7
Monitoring Locations.....	7
Monitoring Equipment .....	7
Monitoring Parameters, Frequency and Duration .....	8
Monitoring Methodology and QA/QC Procedures .....	8
Maintenance and Calibration .....	9
Results and Observations .....	9
<b>3 ENVIRONMENTAL AUDIT.....</b>	<b>10</b>
Environmental Site Audits .....	10
Status of Environmental Licensing and Permitting.....	12
Status of Waste Management.....	12
Implementation Status of Environmental Mitigation Measures .....	12
Implementation Status of Event Action Plans.....	12
Summary of Complaints and Prosecutions .....	13
<b>4 FUTURE KEY ISSUES.....</b>	<b>14</b>
Key Issues for the Coming Month .....	14
Construction Program for the Next Month .....	14
Monitoring Schedule for the Next Month.....	14
<b>5 CONCLUSIONS AND RECOMMENDATIONS.....</b>	<b>15</b>
Conclusions .....	15
Recommendations .....	15

## **LIST OF TABLES**

Table I	Summary Table for Events Recorded in the Reporting Month
Table II	Summary of Key Information in the Reporting Month
Table 1.1	Key Project Contacts
Table 1.2	Monitoring Requirements
Table 2.1	Locations of Noise Monitoring Station
Table 2.2	Noise Monitoring Equipment
Table 2.3	Noise Monitoring Parameters, Frequency and Duration
Table 2.4	Baseline Noise Levels and Allowed Construction Noise Level for Monitoring Table
Table 3.1	Observations and Recommendations of Site Audits
Table 3.2	Environmental License or Permit Obtained in Reporting Month

## **LIST OF FIGURE**

Figure 1.1	Site Layout Plan
Figure 1.2	ET's Organization Chart
Figure 1.3	Project Organization Chart
Figure 2.1	Locations of Construction Noise Monitoring Stations

## **LIST OF APPENDICES**

Appendix A	Action and Limit Levels
Appendix B	Copies of Calibration Certificates
Appendix C	Summary of Exceedance
Appendix D	Noise Monitoring Results and Graphical Presentations
Appendix E	Site Audit Summary
Appendix F	Summary of Waste Generated
Appendix G	Environmental Mitigation Implementation Schedule (EMIS)
Appendix H	Event Action Plans for Construction Noise
Appendix I	Tentative Construction Programme
Appendix J	Environmental Monitoring Schedule

---

## EXECUTIVE SUMMARY

### Introduction

1. This is monthly Environmental Monitoring and Audit (EM&A) Report prepared by Cinotech Consultants Limited (Cinotech) for the Contract No. SS W317 “Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point” (hereinafter called “the Project”). This document reports the findings of the environmental auditing works conducted on June 2010.
2. The site activities undertaken in the reporting month were:
  - T13, T8, T8005, T12, T8008, T8006, T8007, T15, T8009, T8010 and T8011 at CH 0+600 - CH 0+700;
  - T8031, T8032, T8033, T8036, T8038, T8043, T8044, T8049, T8050, T8052, T45, T46, T8055, T8056, T8057, T8058, T8059, T8028, T8029 and T8030 at CH 0 + 700 - CH 0 + 850;
  - T8305, T8308 at CH 850 - CH 960;
  - T191, T8270, T8271, T8272, T8273, T8274, T8275, T8276 and T8277 at CH 1+500 - CH 1+750; &
  - T8278, T8280, T8285, T8286, T8287, T8288, T8289, T8290, T8291, T8292 and T8294 at CH 1+600 - CH 1+700.
  - Tree protection;
  - Tree risk assessment;
  - Excavation Work:- from CH 0+700- CH0+840, CH1+650 to CH 1+870;
  - Fixing reinforcement and formwork:- CH 0+700- CH0+800, CH1+650 to CH1+810; and
  - Placing footing concrete (grade 30/20) :- CH 0+700- CH0+800, CH1+650 to CH 1+810.

### Environmental Monitoring and Audit Works

3. Environmental monitoring and audit works for the Project was commenced on 17 March 2010 in advanced of commencement of construction to monitoring the impact resulted from site preparation work.
4. Environmental monitoring and audit works for the Project is stipulated in the approved EM&A Manual. Site audits were conducted once per week. Environmental site audits were conducted on 2, 9, 15, 23 and 28 Junr 2010. No non-compliance was observed during the site audits.
5. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.
6. Summary of the events and action taken in the reporting month is tabulated in **Table I**.

**Table I Summary Table for Events Recorded in the Reporting Month**

Parameter	No. of Events		No. of Events Due to the Project	Action Taken
	Action Level	Limit Level		
Noise	0	0	0	N/A

**Construction Noise**

7. All construction noise monitoring was conducted as scheduled in reporting month. No Action/Limit Level exceedance was recorded.

**Environmental Licenses and Permits**

8. Licenses/Permits granted to the Project include Environmental Permit, Billing Account under Waste Disposal Ordinance, Notification pursuant to Section 3(1) of the Air Pollution Control Ordinance (Construction Dust) Regulation and Registration as Chemical Waste Producer.

**Key Information in the Reporting Month**

9. Summary of key information in the reporting month are in **Table II**.

**Table II Summary of Key Information in the Reporting Month**

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Complaint received	0	---	N/A	N/A	---
Changes to the assumptions and key construction / operation activities recorded	0	---	N/A	N/A	---
Status of submissions under EP	1	Monthly EM&A Report	Submitted to EPD on 9 June 2010	No Comment	---
	1	Landscape Plan (v 2.1)	Submitted to EPD on 3 June 2010	Resubmit in July	--
Notifications of any summons & prosecutions received	0	---	N/A	N/A	---

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
<b><u>Future Key Issues:</u></b>					
Major site activities for the coming two months include:					
<ul style="list-style-type: none"> <li>• Tree protection;</li> <li>• Tree felling;</li> <li>• Tree survey;</li> <li>• Tree pruning;</li> <li>• Excavation Work:- CH0+300 to CH0+700, CH0+840 to 1+650, CH1+870 to 2+550 &amp; CH2+900 to CH3+300;</li> <li>• Fixing reinforcement and formwork:- CH0+300 to CH0+700, CH0+800 to CH 2+550 &amp; CH1+810 to CH 2+550 &amp; CH2+900 to CH3+300; and</li> <li>• Placing footing concrete (grade 30/20):- CH0+300 to CH0+700, CH0+800 to CH 2+550 &amp; CH1+810 to CH 2+550 &amp; CH2+900 to CH3+300.</li> </ul>					
The anticipated environmental impact will be mainly on noise, dust emission and retaining trees.					

---

## 1 INTRODUCTION

### Background

- 1.1 The Project “Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point” with a Contract No. SS W317 is the Section 1 of the “Construction of a Secondary boundary Fence and new sections of Primary Boundary Fence and Boundary Patrol Road”. Hong Kong Kwong Tai Builders Limited (hereinafter called the “Contractor”) was commissioned by Architectural Services Department (ArchSD) of the Hong Kong Special Administrative Region (HKSAR) to undertake the construction.
- 1.2 The Project mainly comprises a construction purposed to erect a secondary fence along the existing boundary patrol road (approximately 4.1 km) and replace the existing checkpoint at Pak Hok Chau. **Figure 1.1** shown site layout plan.
- 1.3 An Environmental Permit No. EP-347/2009 was issued on 5 June 2009 to the Secretary for Security as the Permit Holder for “Construction of a Secondary Boundary Fence and new sections of Primary Boundary Fence and Boundary Patrol Road”. Later, a Further Environmental Permit (No. FEP-01/347/2009) (hereinafter called the FEP) was issued on 19 February 2010 to Contractor as Permit Holder for the Project. On 9 June 2010, a VEP (EP-347/2009/A) for the whole project was issued to Secretary for Security as the Permit Holder with amendments on the scale and scope of section 4 in whole project.
- 1.4 An environmental impact assessment (EIA) report of the Construction of a Secondary Boundary Fence and new sections of Primary Boundary Fence and Boundary Patrol Road (Register No. AEIAR-136/2009) has been prepared in January 2009.
- 1.5 The Environmental Monitoring and Audit Manual (Project’s EM&A Manual) was also included as part of the EIA report in the register and the Environmental Monitoring & Audit (EM&A) requirements are specified in Section 10. The Contractor shall follow the requirements stipulated in the EM&A requirements when implementing the Project.
- 1.6 Cinotech Consultants Ltd. (Cinotech) was commissioned by the Contractor to undertake the Environmental Monitoring and Audit (EM&A) works for the Project under Condition 2.1 of FEP.
- 1.7 Environmental monitoring and audit works for the Project was commenced at 17 March 2010.
- 1.8 This is monthly EM&A Report summarizing the EM&A works for the Project in June 2010.

## Project Organizations

1.9 Different parties with different levels of involvement in the project organization include:

- The Engineer for the Contract – Mott MacDonald Limited (MMD).
- Contractor – Hong Kong Kwong Tai Builders Limited (HKKT).
- Contractor Environmental Team (CET) – Cinotech Consultants Limited (Cinotech).
- Independent Environmental Checker (IEC) – ENVIRON Hong Kong Limited (ENVIRON).

1.10 The responsibilities of respective parties are provided in Section 2.2 to 2.7 of the EM&A Manual of the Project.

1.11 The key contacts of the Project are shown in Table 1.1.

**Table 1.1 Key Project Contacts**

Party	Name	Role	Phone No.	Fax No.
Engineer	Mr. Danny Wong	Engineer's Representative	28285921	28271923
Contractor	Mr. Alex Cheung	Site Agent	64731088	27894184
	Mr. Tony Lau	Environmental Officer	61807827	
Contractor's ET	Dr. Priscilla Choy	Contractor's Environmental Team Leader (CETL)	2151 2089	3107 1388
	Mr. Gary Lau	Project Coordinator & Audit Team Leader	2151 2098	
	Mr. Henry Leung	Monitoring Team Leader	9779 7340	
IEC	Mr. David Yeung	Independent Environmental Checker (IEC)	3743 0717	3548-6988
	Mr. Simon Lam	Independent Environmental Checker (IEC) Representative	3743 0708	

1.12 The organization chart of ET and the Project are shown in **Figure 1.2** and **1.3** respectively.

## Construction Programme

1.13 The construction activities undertaken in the reporting month were:

- T13, T8, T8005, T12, T8008, T8006, T8007, T15, T8009, T8010 and T8011 at CH 0+600 - CH 0+700;
- T8031, T8032, T8033, T8036, T8038, T8043, T8044, T8049, T8050,



- T8052, T45, T46, T8055, T8056, T8057, T8058, T8059, T8028, T8029 and T8030 at CH 0 + 700 - CH 0 + 850;
- T8305, T8308 at CH 850 - CH 960;
  - T191, T8270, T8271, T8272, T8273, T8274, T8275, T8276 and T8277 at CH 1+500 - CH 1+750; &
  - T8278, T8280, T8285, T8286, T8287, T8288, T8289, T8290, T8291, T8292 and T8294 at CH 1+600 - CH 1+700;
  - Tree protection;
  - Tree risk assessment;
  - Excavation Work:- from CH 0+700- CH0+840, CH1+650 to CH 1+870;
  - Fixing reinforcement and formwork:- CH 0+700- CH0+800, CH1+650 to CH1+810; and
  - Placing footing concrete (grade 30/20) :- CH 0+700- CH0+800, CH1+650 to CH 1+810.

### Summary of EM&A Requirements

1.14 The EM&A programme requires construction phase monitoring for construction noise and environmental site audit. The duties and responsibilities comprise the following:

- monitor various environmental parameters as specified in the EM&A Manual;
- analyze the environmental monitoring and audit data;
- review the EM&A programme to confirm the adequacy and effectiveness of mitigation measures implemented and the validity of the EIA predictions and to identify and adverse environmental impacts arising;
- carry out site inspection to investigate and audit the Contractor's site practice, equipment and work methodologies with respect to pollution control and environmental mitigation, and effect proactive action to pre-empt problems;
- audit and prepare EM&A reports on the site environmental conditions;
- report the environmental audit results to the Contractor;
- recommend appropriate mitigation measures to the Contractor in case of exceedance of Action and Limit Levels in accordance with the Event and Action Plans

1.15 Summary of monitoring requirements are shown in the table below:

**Table 1.2 Monitoring Requirements**

Monitoring Station	Parameter (Noise), dB(A)	Period	Frequency	Measurement
VH 01 and VH 03	L <sub>10</sub> (30 min.) L <sub>90</sub> (30 min.) L <sub>eq</sub> (30 min.)	07:00-19:00 hours on normal weekdays (During construction)	Once per week	Façade

- 1.16 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 3 of this report.
- 1.17 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the required monitoring parameters, namely noise levels and audit works for the Project in June 2010.

## 2 NOISE

### Monitoring Requirements

- 2.1 In accordance with the EM&A Manual, two noise monitoring stations (VH01 and VH03) out of ten noise monitoring stations in EIA report were considered representative for Section 1 and designated for impact noise monitoring. **Appendix A** shows the established Action/Limit Levels for the environmental monitoring works.

### Monitoring Locations

- 2.2 **Table 2.1** describes the locations of the monitoring stations and their locations are shown in **Figure 2.1**.

**Table 2.1 Locations of Noise Monitoring Stations**

Monitoring Station	Location
VH01	Village House at Mai Po
VH03	

### Monitoring Equipment

- 2.3 **Table 2.2** summarizes the noise monitoring equipment models being used. Copies of calibration certificates are attached in **Appendix B**.

**Table 2.2 Noise Monitoring Equipment**

Equipment	Model and Make	Quantity
Integrating Sound Level Meter	SVAN 959 /955	1
Calibrator	B&K4231 / SV30A	1

**Monitoring Parameters, Frequency and Duration**

2.4 **Table 2.3** summarizes the monitoring parameters, frequency and total duration of monitoring.

**Table 2.3 Noise Monitoring Parameters, Frequency and Duration**

<b>Monitoring Station</b>	<b>Time Period</b>	<b>Frequency</b>	<b>Parameter</b>	<b>Method</b>
VH01 and VH03	0700-1900 hrs on weekdays	Once per week	$L_{eq}(30min.)$ dB(A) $L_{10}(30min.)$ dB(A), & $L_{90}(30min.)$ dB(A)	Façade measurement

**Monitoring Methodology and QA/QC Procedures**

- The microphone head of the head level meter should position 1m exterior of the noise sensitive facade and lowered sufficiently so that the building's external wall acts as a reflecting surface.
- The battery condition should check to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
  - frequency weighting : A
  - time weighting : Fast
  - time measurement : 30 minutes / 5 minutes
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1000 Hz. If the difference in the calibration level before and after measurement was more than 1 dB(A), the measurement was considered invalid and repeat of noise measurement was required after re-calibration or repair of the equipment.
- The wind speed was frequently checked with the portable wind meter.
- At the end of the monitoring period, the  $L_{eq}$ ,  $L_{90}$  and  $L_{10}$  were recorded. In addition, site conditions and noise sources were record on a standard record sheet.
- Noise measurement was paused during periods of high intrusive noise if possible and observation was recorded when intrusive noise was not avoided.
- Noise monitoring was cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s.

---

**Maintenance and Calibration**

2.5 Maintenance and Calibration procedures were as follows:

- The microphone head of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.
- The meter and calibrator would send to laboratory to check and calibrate at yearly intervals.

**Results and Observations**

2.6 All construction noise monitoring at two designated locations were conducted as scheduled in the reporting month. The Monitoring scheduled is shown in **Appendix J**.

2.7 No Action/Limit Level exceedance was recorded in the reporting month. Summary of exceedance is shown in **Appendix C**.

2.8 The effects of weather condition on the monitoring results are insignificant and the major noise source identified for these monitoring stations was road traffic noise. Weather condition, noise monitoring results and graphical presentations are shown in **Appendix D**.

2.9 In accordance with Condition 5.2 of the EP, all environmental monitoring data was made available to the public via internet access at the website <http://www.cinotech.com.hk/projects/SBF>.

2.10 All the Construction Noise Levels (CNLs) reported in this report had been adjusted with the corresponding baseline levels (i.e. Measured Leq – Baseline Leq = CNL), in order to facilitate the interpretation of the noise exceedance. The baseline noise level and the allowed CNL at each construction noise monitoring station are presented in **Table 2.4**.

**Table 2.4 Baseline Noise Levels and Allowed Construction Noise Level (CNL) for the Monitoring Stations**

Station	Baseline Noise Level, dB (A)	Allowed CNL, dB (A)
VH01 Villager House	56.4	75
VH03 Villager House	49.8	75

### 3 ENVIRONMENTAL AUDIT

#### Environmental Site Audits

- 3.1 Environmental site audits were carried out on weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.
- 3.2 Site audits for the Project in the reporting month were conducted on 2, 9, 15, 23 and 28 June 2010. No non-compliance was observed during the site audits.
- 3.3 Site inspections were undertaken to ensure and check the compliance with the FEP and that the implementation and maintenance of air quality, water quality, ecology and landscape and visual mitigation measures are being properly carried out in the reporting month in accordance to section 3.2, 5.2, 6.2 and 7.3 of the EM&A Manual respectively. No non-compliance was observed during the site inspections.
- 3.4 No excavation works were observed within the 150m buffer zone from Tam Kon Chau Egretty in accordance with Condition 3.2 of the FEP.
- 3.5 The summaries of site audits are attached in **Appendix E**.
- 3.6 During site inspections in the reporting month, no non-conformance was identified. The observations and recommendations are summarized in **Table 3.1**.
- 3.7 Proactive liaison with the contractor and close monitoring of contractor's work practices will be undertaken to ensure environmental mitigation measures are fully implemented and environmental deficiencies observed during site inspections are rectified promptly..

**Table 3.1 Observations and Recommendations of Site Audits**

Parameters	Date (Ref. no.)	Observations	Remediation/ Follow up
Air Quality	15-06-10 (00615-R(3))	Mud trail was observed near the wheels washing bay at gate No. 40. Contractor was reminded to clear it regularly.	The situation was observed outstanding and remarked as item 000623-R(5) on 23-06-10.
	23-06-10 (00623-R(4))	Exposed stockpile was observed next to gate No.34. Contractor was reminded to cover it with tarpaulin.	The situation was observed outstanding and remarked as item 000628-R(3) on 28-06-10.
	23-06-10 (00623-R(5))	Mud trail was observed at access road. Contractor was reminded to remove it regularly.	The situation was improved / rectified on 28-06-10.
	28-06-10 (00628-R(3))	Exposed stockpile was observed next to gate No.34. Contractor was reminded to cover it with tarpaulin.	The situation will be followed up during coming audit sessions.

Water Quality	02-06-10 (00602-R(2))	To cover the excavated area with geo-textile to prevent surface run-off occur near the fish pond.	The situation was observed outstanding and remarked as item 000609-O(1) on 09-06-10.
	09-06-10 (00609-R(3))	Over flow was observed at wheels washing Bay. Contractor was reminded to remove the water regularly especially after raining.	The situation was improved / rectified on 15-06-10.
	23-06-10 (00623-R(2))	To fill the wheels washing bay with sufficient water and desilting the water regularly.	The situation was improved / rectified on 28-06-10.
	23-06-10 (00623-R(3))	To cover the slope next to fish pond to prevent surface run-off occur during rainstorm.	The situation was observed outstanding and remarked as item 000628-R(2) on 28-06-10.
	28-06-10 (00628-R(2))	To cover the slope next to fish pond to prevent surface run-off occur during rainstorm.	The situation will be followed up during coming audit sessions.
Landscape and Visual	02-06-10 (00602-R(1))	To erect protection fence surrounding the remaining retaining trees.	The situation was observed outstanding and remarked as item 000609-R(1) on 09-06-10.
	09-06-10 (00609-R(1))	To erect protection fence surrounding the remaining retaining trees.	The situation was observed outstanding and remarked as item 000615-R(1) on 15-06-10.
	09-06-10 (00609-R(2))	Removal of protection fence is observed. Contractor was reminded to maintain the fence surrounding the retaining trees.	The situation was observed outstanding and remarked as item 000615-R(2) on 15-06-10.
	15-06-10 (00615-R(1))	To erect protection fence surrounding the remaining retaining trees.	The situation was observed outstanding and remarked as item 000623-R(1) on 23-06-10.
	15-06-10 (00615-R(2))	Removal of protection fence is observed. Contractor was reminded to maintain the fence surrounding the retaining trees.	The situation was observed outstanding and remarked as item 000623-R(1) on 23-06-10.
	23-06-10 (00623-R(1))	Removal of protection fence is observed. Contractor was reminded to erect and maintain the regularly.	The situation was improved / rectified on 28-06-10.
	28-06-10 (00628-R(1))	To maintain the protection fencing around the retaining tree regularly.	The situation will be followed up during coming audit sessions.
	28-06-10 (00628-R(4))	To remove the felled tree immediately after tree felling process to prevent damage made on retaining trees.	The situation will be followed up during coming audit sessions.
Waste / Chemical Management	23-06-10 (00623-R(6))	Chemical containers were observed without proper storage. Contractor was reminded to provide drip tray to contain them.	The situation was improved / rectified on 28-06-10.

**Status of Environmental Licensing and Permitting**

3.8 Environmental license or permit obtained in the reporting month is shown in **Table 3.2**.

**Table 3.2 Environmental License or Permit Obtained in Reporting Month**

Type of License/ Permit	Number	Valid Period		Details	Status
		From	To		
VEP	EP-347 /2009/A	15/06/2010	N/A	Location: Boundary patrol road between Mai Po and Lok Ma Chau Control Point	Vaild
FEP	FEP-01/347/2009	19/02/2010	N/A		Vaild
Registration as Chemical Waste Producer	5213-542-H3263-02	29/03/2010	N/A	i) Location of waste is produced: Border Road, Yuen Long ii) Major chemical waste: Waste paint drum, waste paint can and waste paint.	Vaild
Billing Account under Waste Disposal Ordinance	7010229	11/02/2010	N/A	Disposal of construction and demolition waste under Waste Disposal Ordinance	Valid
Notification pursuant	314415	23/02/2010	N/A	Notification pursuant to Section 3(1) of the Air Pollution Control Ordinance (Construction Dust) Regulation	N/A

**Status of Waste Management**

3.9 The amount of waste generated by the construction activities of the Project in the reporting month is shown in **Appendix F**.

**Implementation Status of Environmental Mitigation Measures**

3.10 According to the Environmental Permit and the EM&A Manual, the mitigation measures detailed in the documents are required to be implemented. Details of implementation Status of Environmental Mitigation Measures are provided in **Appendix G**.

**Implementation Status of Event Action Plans**

3.11 The Event Action Plans for construction noise are presented in **Appendix H**.

Construction Noise

3.12 No Action/Limit Level exceedance was reported in the reporting month.

**Summary of Complaints and Prosecutions**

3.13 No environmental complaint and prosecution related to the Project works was received in the reporting month.



## **4 FUTURE KEY ISSUES**

### **Key Issues for the Coming Month**

4.1 Key issues to be considered in the coming month include:

- Tree protection;
- Tree felling;
- Tree survey;
- Tree pruning;
- Excavation Work:- CH0+300 to CH0+700, CH0+840 to 1+650, CH1+870 to 2+550 & CH2+900 to CH3+300;
- Fixing reinforcement and formwork:- CH0+300 to CH0+700, CH0+800 to CH 2+550 & CH1+810 to CH 2+550 & CH2+900 to CH3+300; and
- Placing footing concrete (grade 30/20):- CH0+300 to CH0+700, CH0+800 to CH 2+550 & CH1+810 to CH 2+550 & CH2+900 to CH3+300.

### **Construction Program for the Next Month**

4.2 The tentative construction program for the Project is provided in **Appendix I**.

### **Monitoring Schedule for the Next Month**

4.3 The tentative environmental monitoring schedule for coming month for the Project is provided in **Appendix J**.

## **5 CONCLUSIONS AND RECOMMENDATIONS**

### **Conclusions**

- 5.1 Five environmental site audits were performed in June 2010. No non-compliance was observed during the site audits.
- 5.2 All construction noise monitoring was conducted as scheduled in the reporting month. All monitoring results were checked and reviewed. No Action/Limit Level exceedance was recorded.
- 5.3 No environmental complaint and prosecution related to the project was received in the reporting month.

### **Recommendations**

- 5.4 According to the environmental audits performed in the reporting month, the following recommendations are recommended:

#### *Dust Impact*

- To ensure water spray is applied for the dust emissive works, such as breaking, loading and unloading of soil materials;
- To implement dust suppression measures on haul road, stockpiles and dry surfaces.

#### *Noise Impact*

- To space out noisy equipment and position as far away as possible from sensitive receivers.
- To review the works sequence of site activities so as to reduce the number of noisy equipment in concurrent operation.
- To provide temporary noise barriers for noisy activities, such as breaking works and drilling works.
- To employ quiet powered mechanical equipment if possible.
- To ensure compliance of CNP conditions during restricted-hour works.

#### *Water Quality Impact*

- To identify any wastewater discharges from site;
- To regularly maintain the condition of u-channel, catch pits and wheel washing facilities on site;

- To regularly maintain the sediment control measures after rainstorms;
- To avoid water from accumulation on site and carry out larviciding against mosquito breeding for stagnant water when mosquito larvae are observed;
- To ensure wastewater removed by dumps from the U-channels to prevent flooding and over flow.

*Waste/Chemical Management*

- To check for any accumulation of waste materials or rubbish on site;
- To avoid any discharge of chemical waste or oil directly from the site;
- To well maintain the equipments and drip trays to avoid oil leakage;
- To avoid improper handling or storage of oil and paint drum on site.

*Landscape*

- To maintain the protection fencing surround the retaining trees;
- To remove the felled tree to avoid damage on retaining trees.


---


---

**FIGURE**


---

---

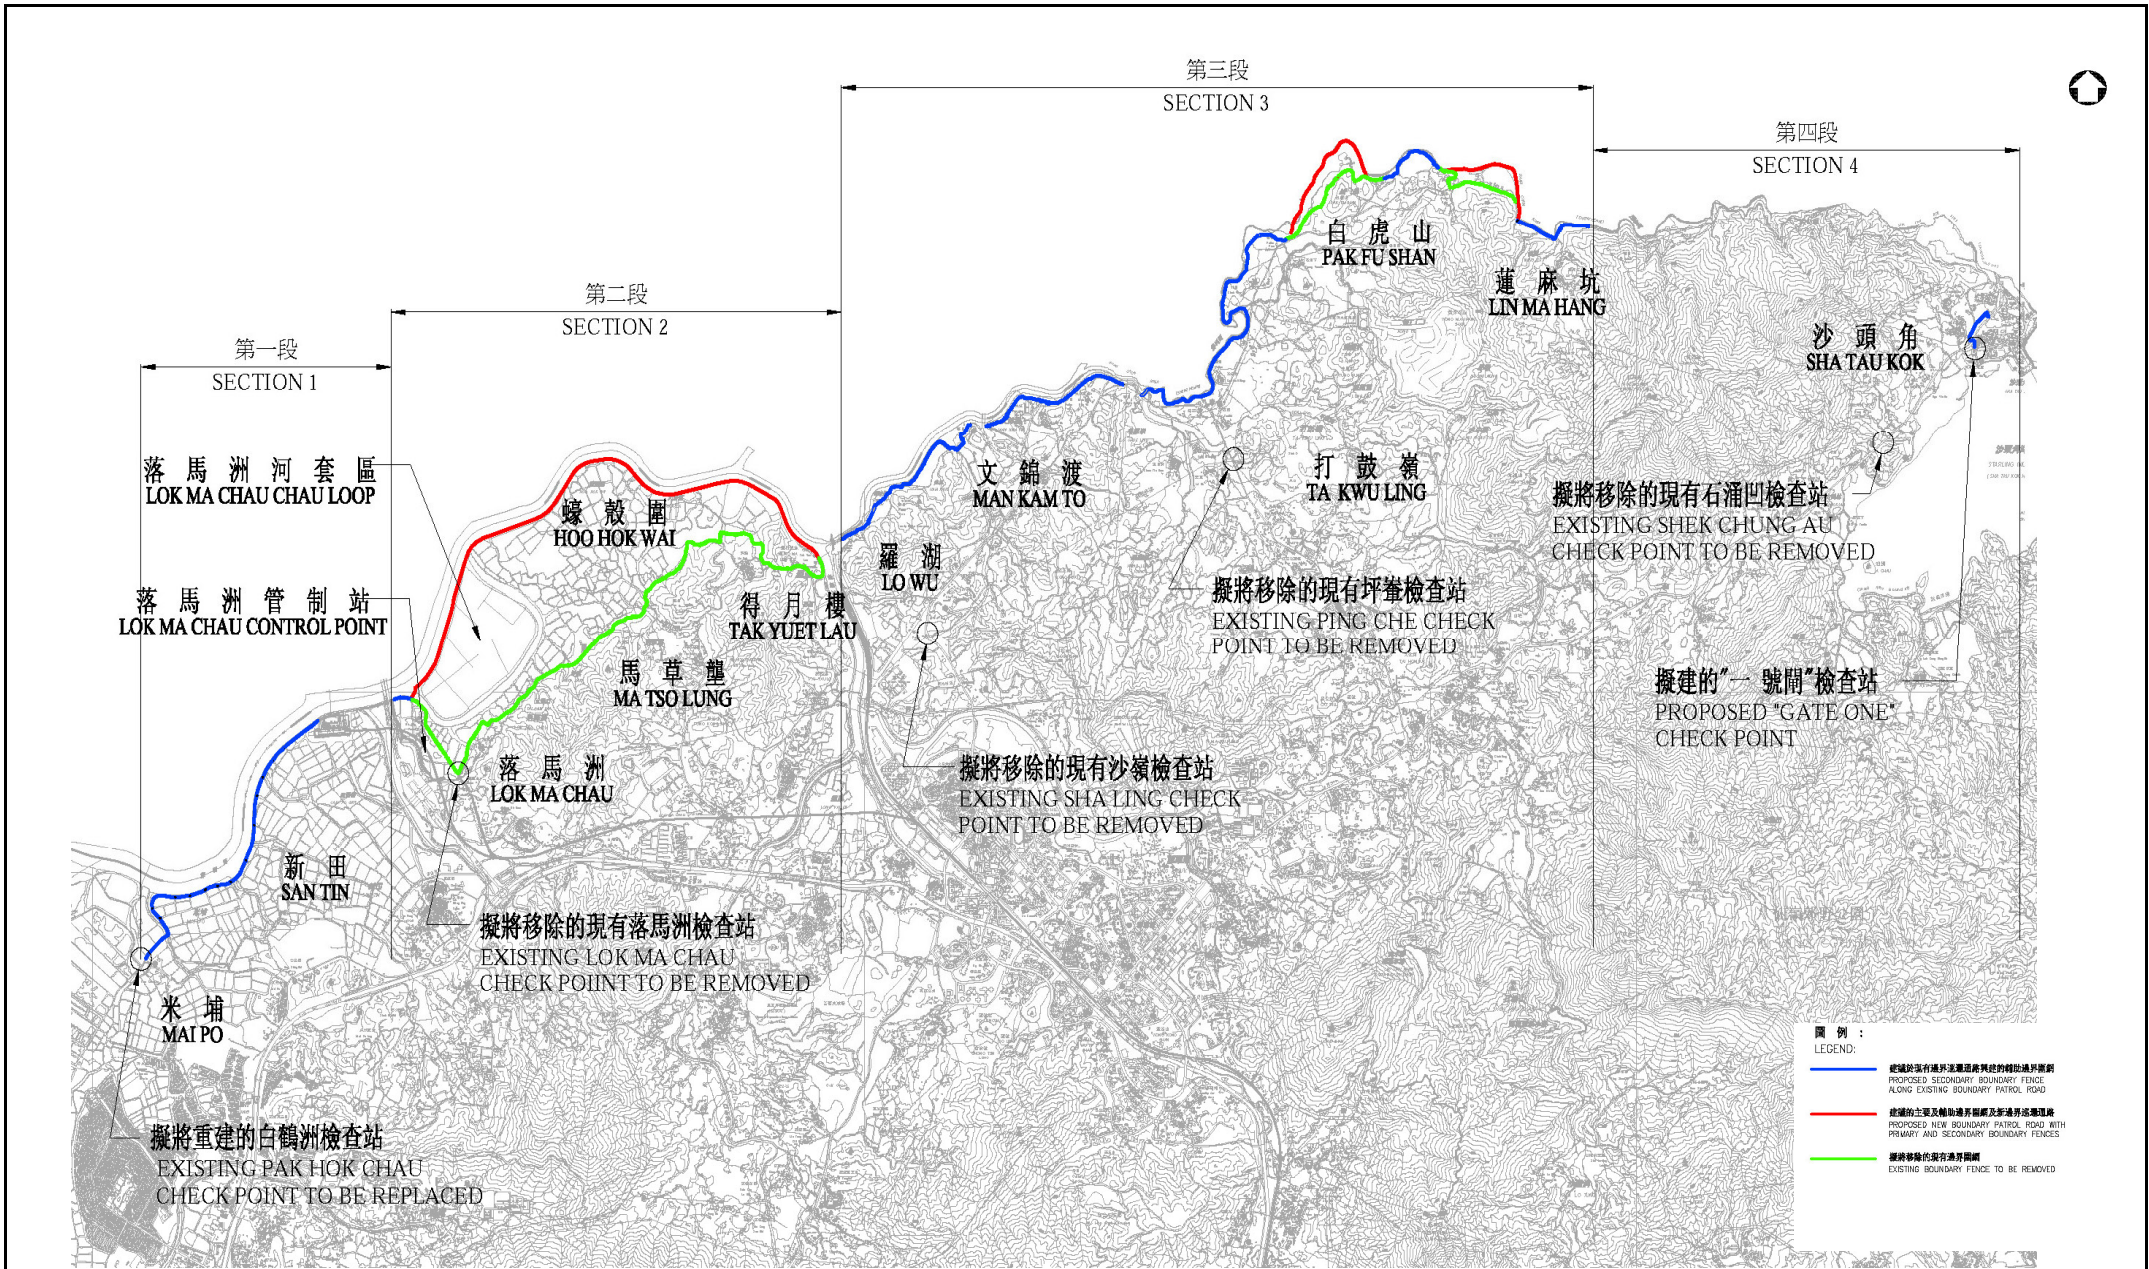

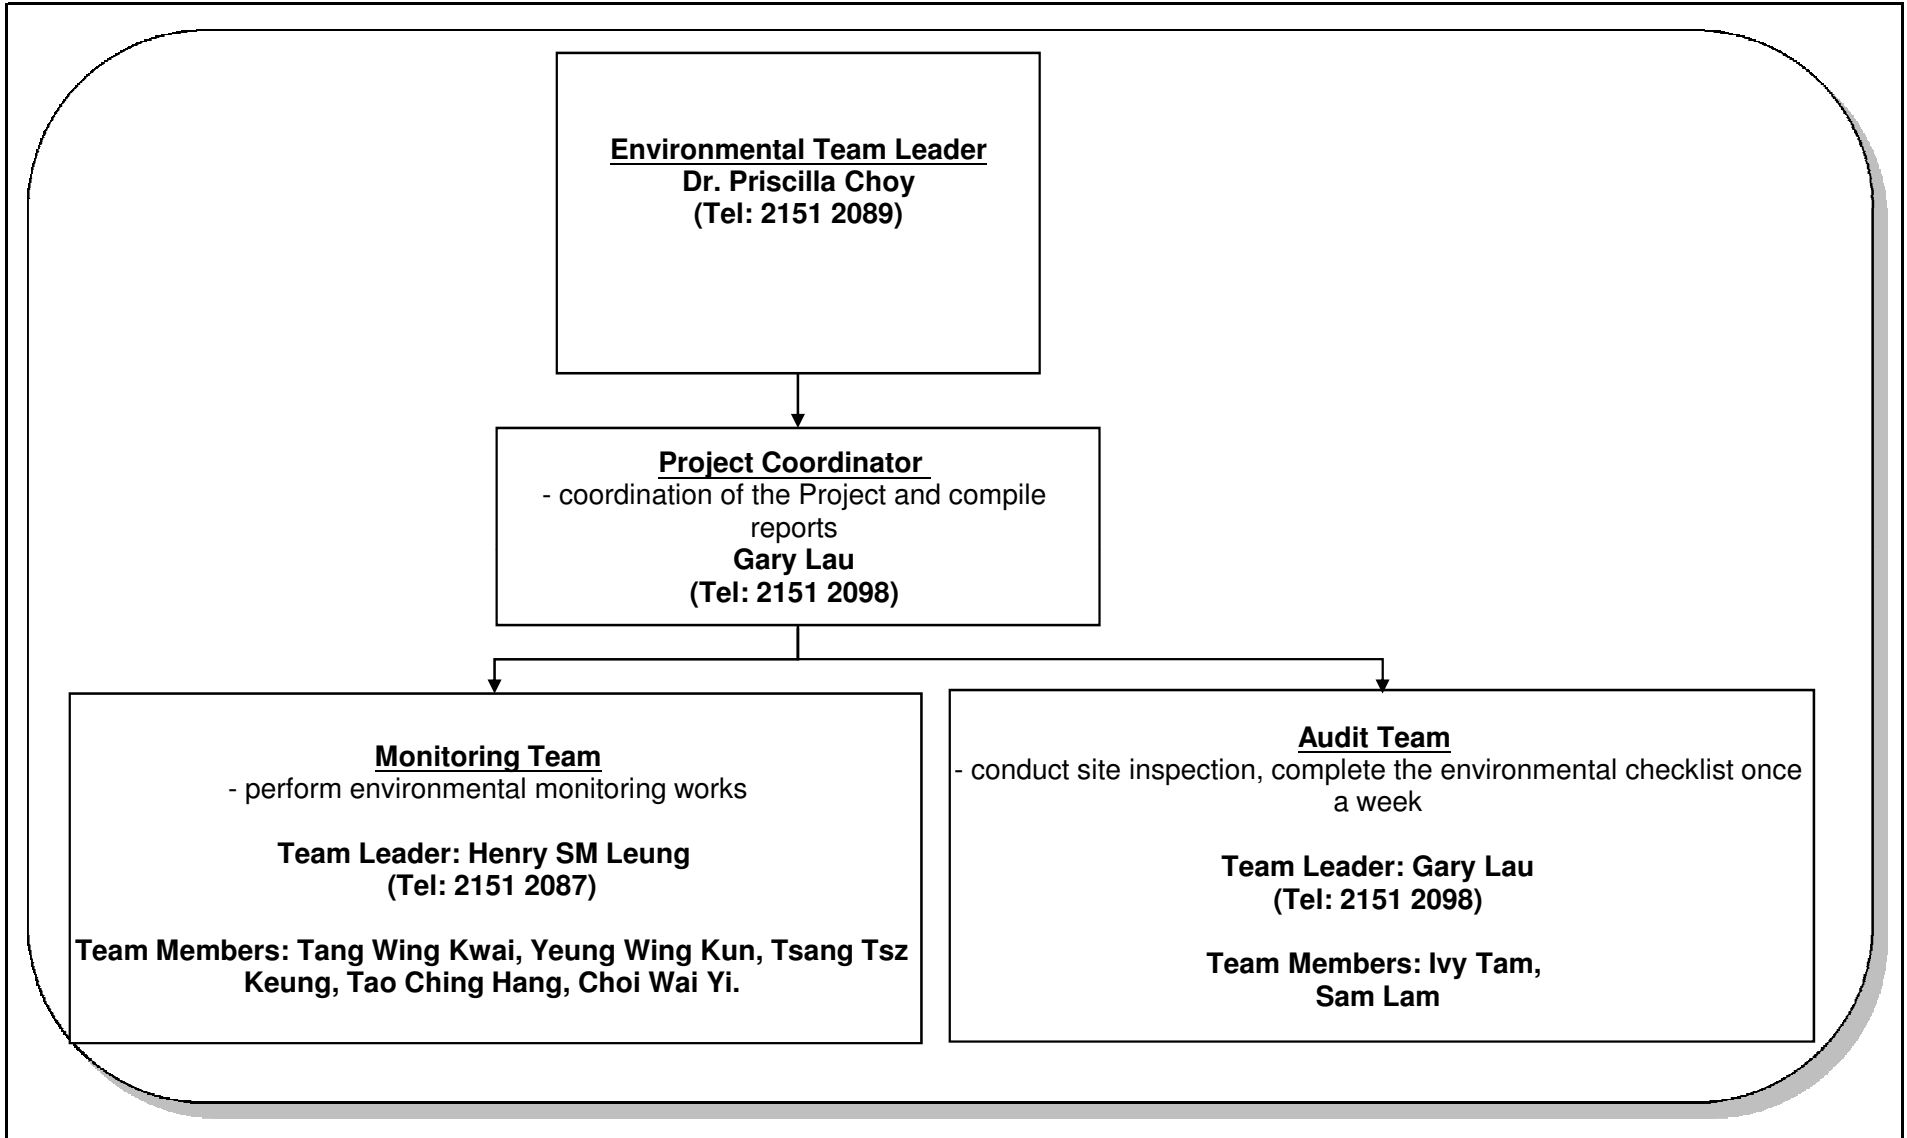


Title	Contract No: SSW 317 Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point  ET Organization Chart	Scale	N.T.S	Project No.	MA0001	CINOTECH
		Date	Jun-10	Figure	1.2	

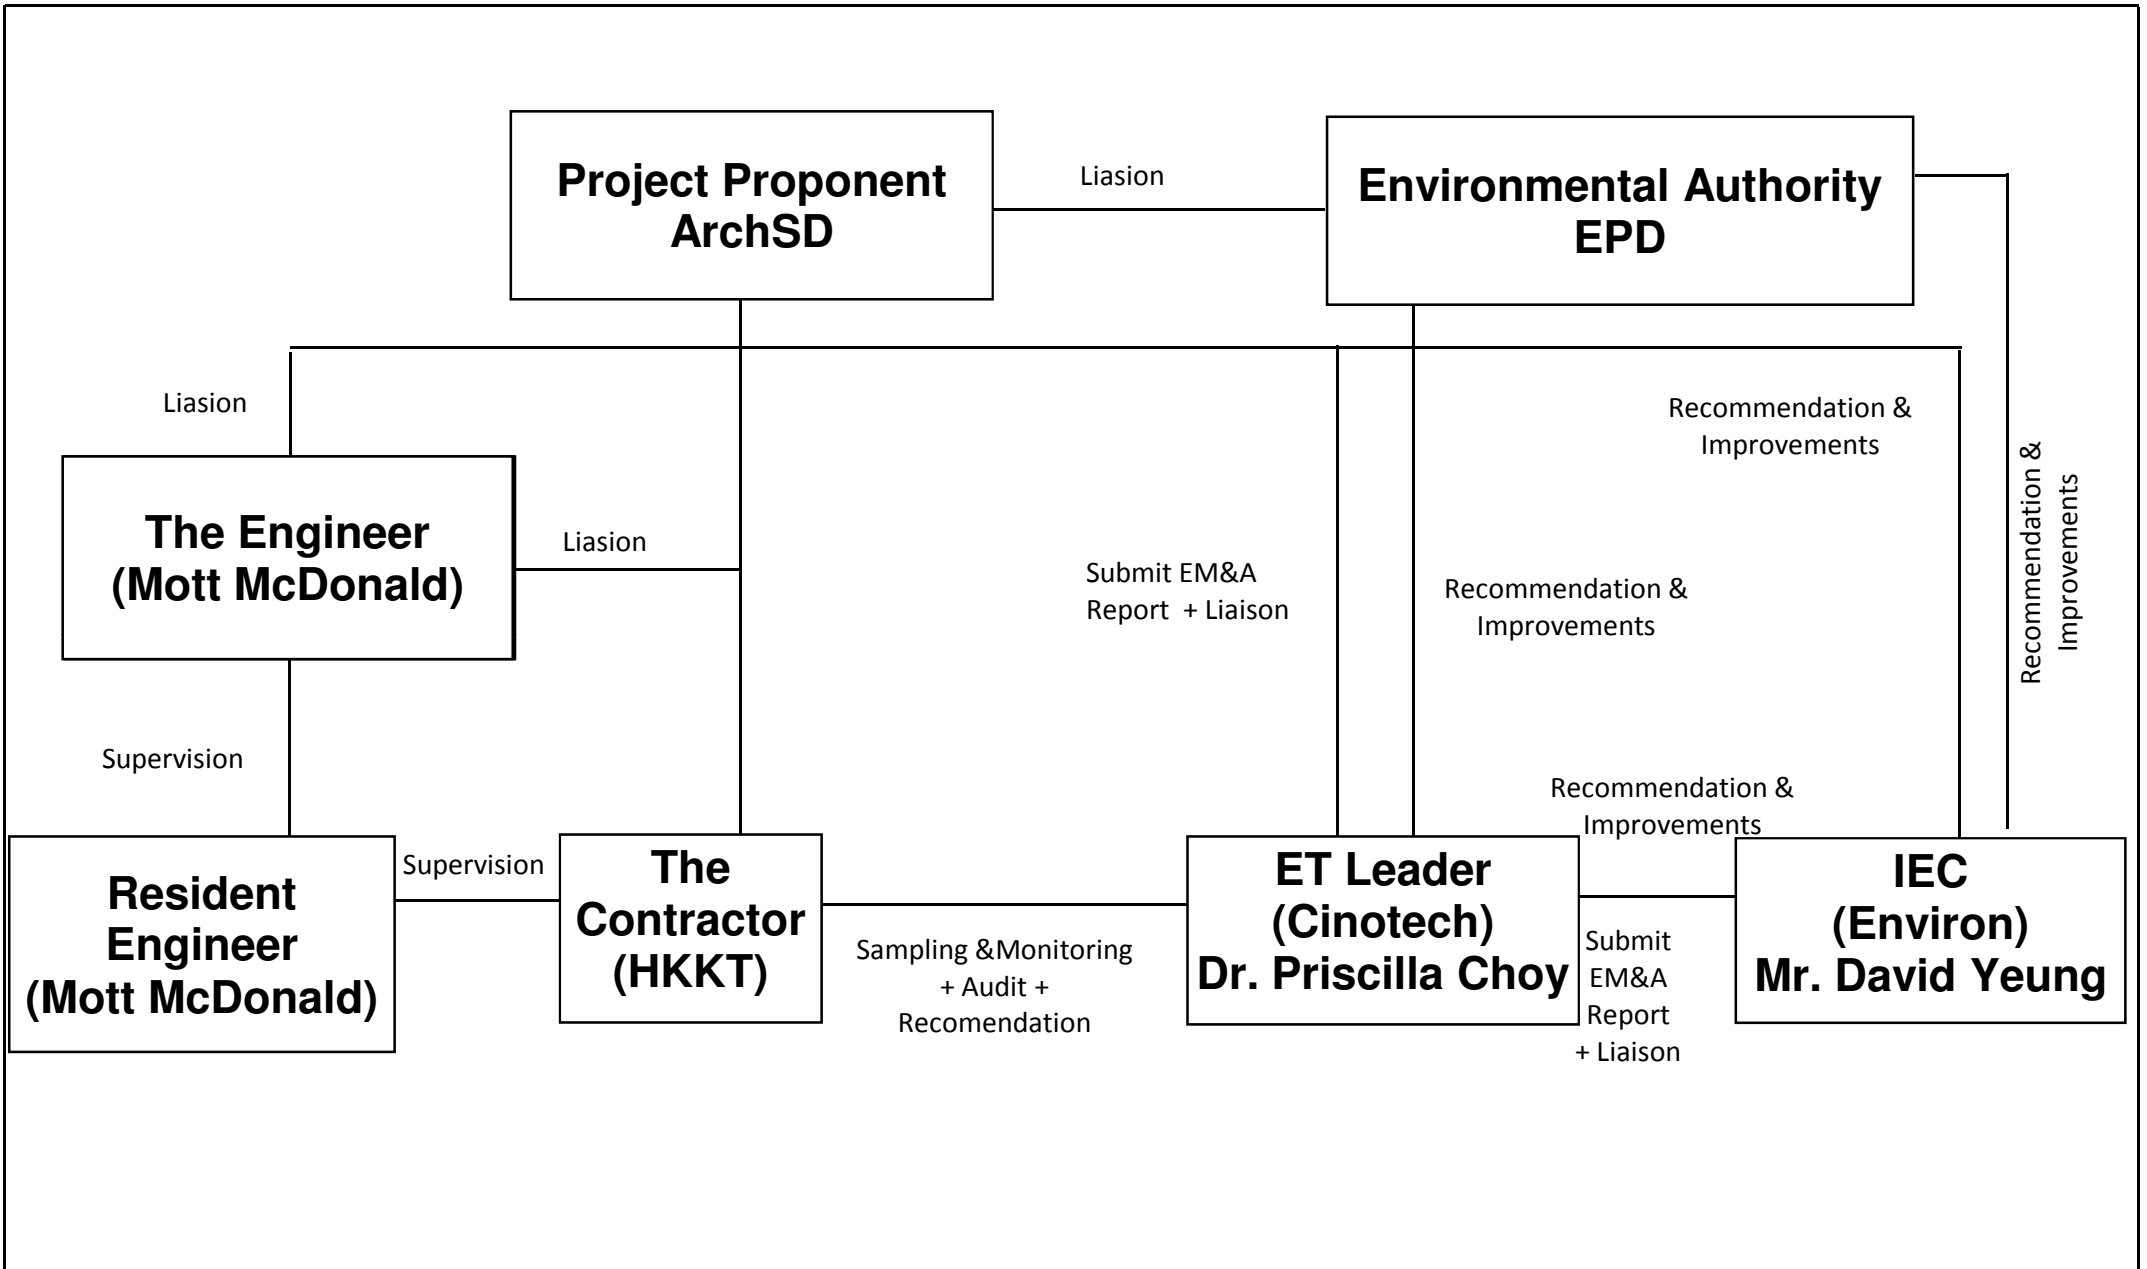

Title	Contract No. SS W317 Construction of a Secondary Fence from Mai Po to Lok Ma Chau Control Point	Scale	N.T.S	Project No.	MA0001	CINOTECH
		Date	Apr-10	Figure	1.3	

Organization Chart of Project



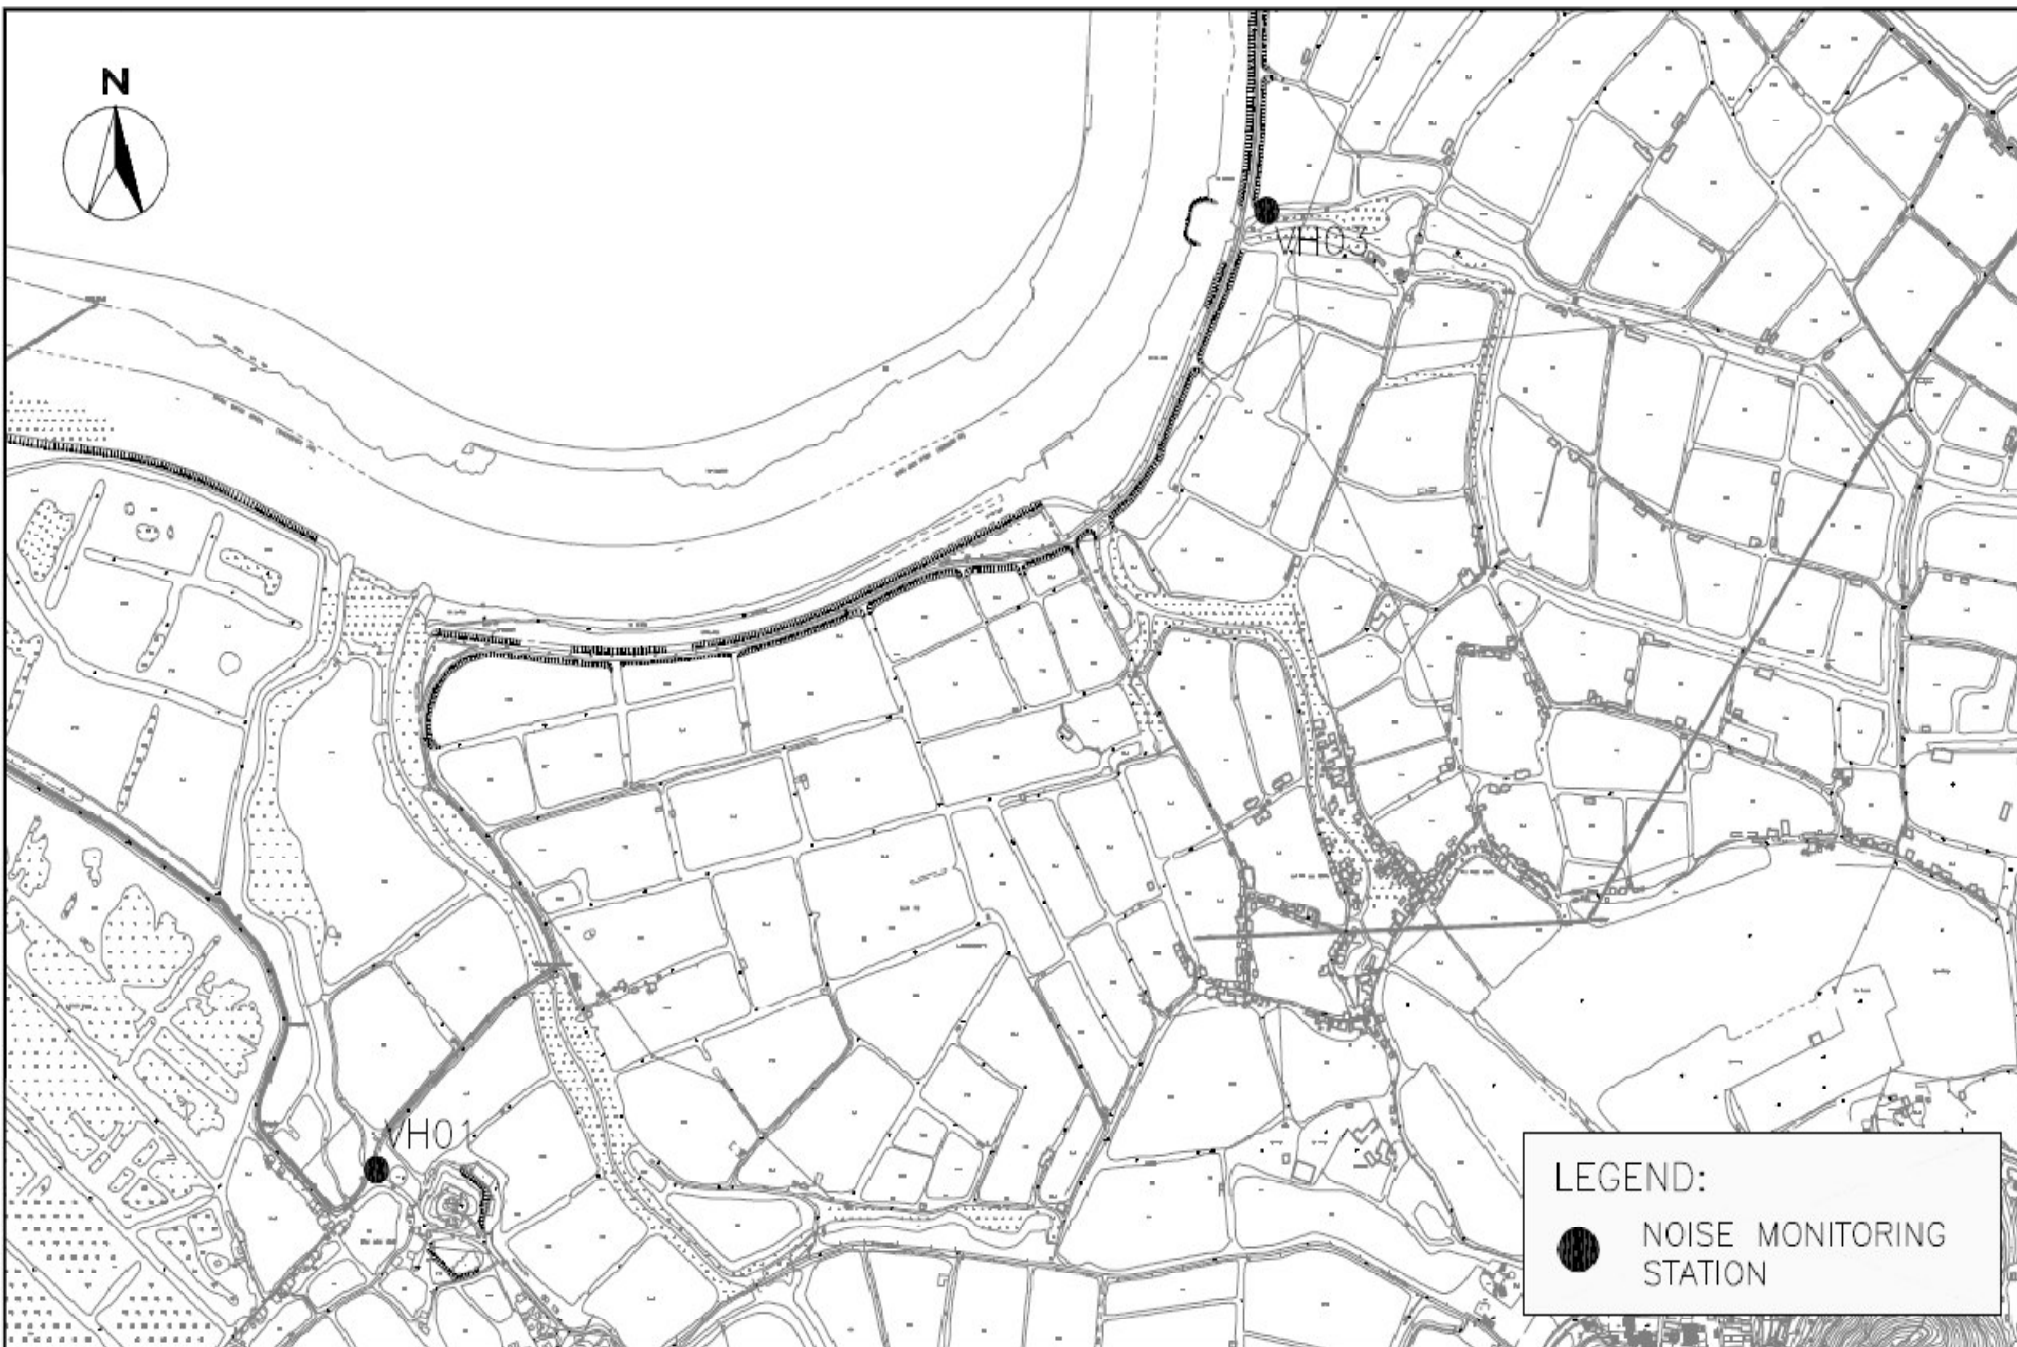

LEGEND:

● NOISE MONITORING STATION



Contract No. SSW317  
Construction of a Secondary Boundary Fence from Mai Po to  
Lok Ma Chau Control Point

### LOCATION OF NOISE MONITORING STATIONS

SCALE	N.T.S.	DATE	FEB 2010
CHECK	CH	DRAWN	SL
JOB No.	MA0001	FIGURE NO.	2.1
		REV	-



---

---

**APPENDIX A  
ACTION AND LIMIT LEVELS**

---

---

**Appendix A - Action and Limit Level for Construction Noise**

<b>Time Period</b>	<b>Action Level</b>	<b>Limit Level</b>
0700-1900 hrs on normal weekdays	When one documented complaint is received	75 dB(A)

---

---

**APPENDIX B  
COPIES OF CALIBRATION  
CERTIFICATES**

---

---

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/90925/4
Date of Issue:	2009-09-25
Date Received:	2009-09-24
Date Tested:	2009-09-24
Date Completed:	2009-09-25
Next Due Date:	2010-09-24

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description : 'SVANTEK' Integrating Sound Level Meter  
Manufacturer : SVANTEK  
Model No. : SVAN 955  
Serial No. : 12553  
Microphone No. : 35222  
Equipment No. : N-08-02

**Test conditions:**

Room Temperature : 23 degree Celsius  
Relative Humidity : 58%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**

In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
\_\_\_\_\_  
**PATRICK TSE**  
*Laboratory Manager*

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/100123/1
Date of Issue:	2010-01-23
Date Received:	2010-01-22
Date Tested:	2010-01-23
Date Completed:	2010-01-23
Next Due Date:	2011-01-22

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Certificate of Calibration

**Item for calibration:**

Description	: 'SVANTEK' Integrating Sound Level Meter
Manufacturer	: SVANTEK
Model No.	: SVAN 955
Serial No.	: 14303
Microphone No.	: 17204
Equipment No.	: N-08-05

**Test conditions:**

Room Temperature	: 21 degree Celsius
Relative Humidity	: 56%

**Test Specifications:**

Performance checking at 94 and 114 dB

**Methodology:**


In-house method, according to manufacturer instruction manual

**Results:**

Reference Set Point, dB	Instrument Readings, dB
94	94.0
114	114.0

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
**PATRICK TSE**  
Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/90925/2
Date of Issue:	2009-09-25
Date Received:	2009-09-24
Date Tested:	2009-09-24
Date Completed:	2009-09-25
Next Due Date:	2010-09-24

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: SVANTEK
Model No.	: SV30A
Serial No.	: 10929
Equipment No.	: N-09-01

### Test conditions:

Room Temperature	: 23 degree Celsius
Relative Humidity	: 58%

### Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

### Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**



**PATRICK TSE**

Laboratory Manager

## TEST REPORT

**APPLICANT:** Cinotech Consultants Limited  
Room 1710, Technology Park,  
18 On Lai Street,  
Shatin, NT, Hong Kong

Test Report No.:	C/N/91109/1
Date of Issue:	2009-11-09
Date Received:	2009-11-07
Date Tested:	2009-11-07
Date Completed:	2009-11-09
Next Due Date:	2010-11-08

**ATTN:** Mr. Henry Leung

Page: 1 of 1

### Item for calibration:

Description	: Acoustical Calibrator
Manufacturer	: SVANTEK
Model No.	: SV30A
Serial No.	: 10965
Equipment No.	: N-09-02

### Test conditions:

Room Temperature	: 21 degree Celsius
Relative Humidity	: 55%

### Methodology:

The Sound Level Calibrator has been calibrated in accordance with the documented procedures and using standard(s) and instrument(s) which are recommended by the manufacturer, or equivalent.

### Results:

Sound Pressure Level (1kHz)	Measured SPL	Tolerance
At 94 dB SPL	94.0	94.0 ± 0.1 dB
At 114 dB SPL	114.0	114.0 ± 0.1 dB

*PREPARED AND CHECKED BY:*

For and On Behalf of **WELLAB Ltd.**

  
\_\_\_\_\_  
**PATRICK TSE**  
Laboratory Manager

---

---

**APPENDIX C  
SUMMARY OF EXCEEDANCE**

---

---



**Appendix C – Summary of Exceedance**

**Reporting Month:** June 2010

**Exceedance Report for Construction Noise (NIL)**

---

---

**APPENDIX D  
NOISE MONITORING RESULTS AND  
GRAPHICAL PRESENTATIONS**

---



---

## Appendix D - Noise Monitoring Results

Location VH01 - Village House at Mai Po							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
1-Jun-10	10:00	Cloudy	46.8	49.8	42.5	56.4	46.8 Measured ≤ Baseline
9-Jun-10	09:00	Cloudy	48.2	50.5	46.5		48.2 Measured ≤ Baseline
15-Jun-10	15:30	Sunny	47.9	49.5	43.0		47.9 Measured ≤ Baseline
22-Jun-10	13:00	Sunny	47.4	49.5	44.0		47.4 Measured ≤ Baseline
29-Jun-10	09:00	Cloudy	48.1	49.5	44.5		48.1 Measured ≤ Baseline

Location VH03 - Village House at Mai Po							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L <sub>eq</sub>	L <sub>10</sub>	L <sub>90</sub>	L <sub>eq</sub>	L <sub>eq</sub>
1-Jun-10	10:45	Cloudy	45.7	48.3	43.0	49.8	45.7 Measured ≤ Baseline
9-Jun-10	09:45	Cloudy	48.9	51.0	45.5		48.9 Measured ≤ Baseline
15-Jun-10	16:10	Sunny	47.6	49.0	43.5		47.6 Measured ≤ Baseline
22-Jun-10	13:45	Sunny	46.3	48.5	42.5		46.3 Measured ≤ Baseline
29-Jun-10	09:45	Cloudy	47.6	49.0	44.0		47.6 Measured ≤ Baseline

## Noise Levels

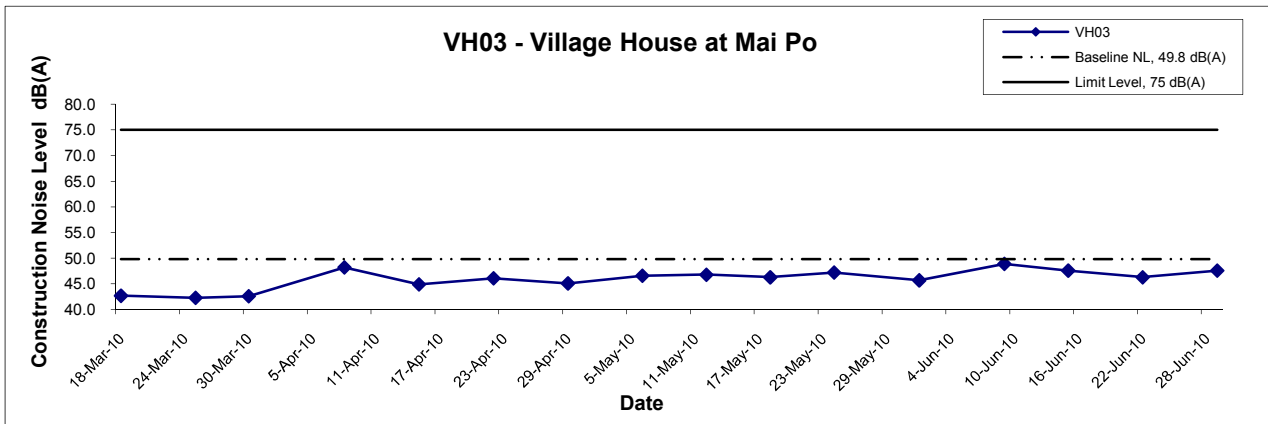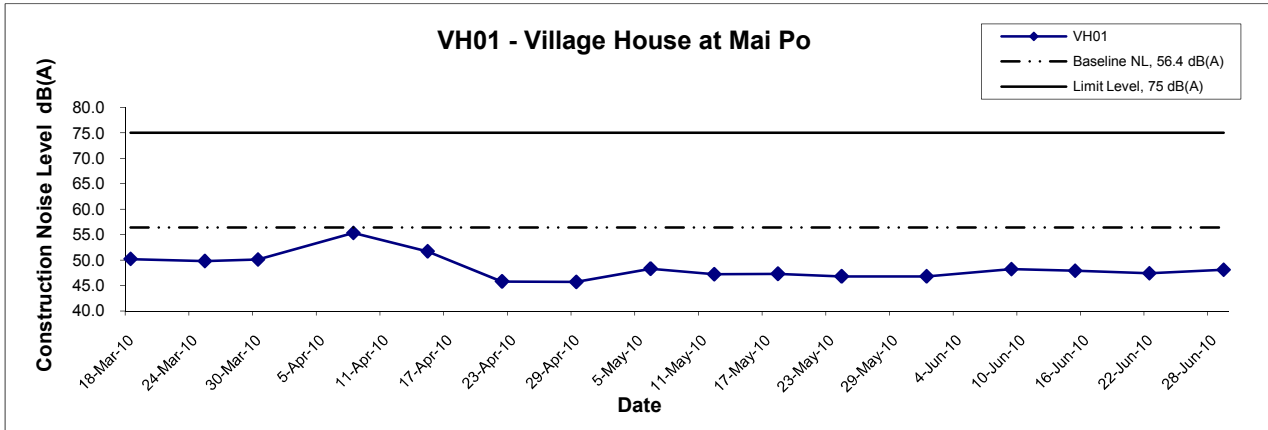

Title Contract No. SSW317 Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point  Graphical Presentation of Construction Noise Monitoring Results	Scale N.T.S	Project No. MA0001	
	Date Jun 10	Appendix D	

---

---

**APPENDIX E**  
**SITE AUDIT SUMMARY**

---

---

Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	00602
Date	2 June 2010 (Wednesday)
Time	14:30-15:30

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>B. Water Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>C. Air Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>D. Noise</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>E. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Landscape</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>G. Permits/Licences</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>H. Others</b>	
	• No environmental deficiency was identified during site inspection.	

	Reminders	Related Item No.
	The Contractor was reminded to implement the following preventive measures:	
	<b>B. Water Quality</b>	
00602-R(2)	• To cover the excavated area with geo-textile to prevent surface run-off occur near the fish pond.	B 13
	<b>C. Air Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>D. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>E. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Landscape</b>	
00602-R(1)	• To erect protection fence surrounding the remaining retaining trees.	F 1
	<b>G. Permits/Licences</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>H. Others</b>	
	• Environmental deficiencies were not rectified/improved by the Contractor during the site inspection: item 00525-R(1) is remarked as item 00602-R(1)	

	Name	Signature	Date
Recorded by	Gary Lau		7 June 2010
Checked by	Dr. Priscilla Choy		7 June 2010

Inspection Information

Checklist Reference Number	00609
Date	9 June 2010 (Wednesday)
Time	14:30-15:45



Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>B. Water Quality</b>	
00609-001	<ul style="list-style-type: none"> <li>To cover the excavated area with geo-textile to prevent surface run-off occurs near the fish pond.</li> </ul>	B 11 and B 13
	<b>C. Air Quality</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>D. Noise</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>E. Waste / Chemical Management</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>F. Landscape</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>G. Permits/Licences</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>H. Others</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	

	Reminders	Related Item No.
	The Contractor was reminded to implement the following preventive measures:	
	<b>B. Water Quality</b>	
00609-R(3)	<ul style="list-style-type: none"> <li>Over flow was observed at wheels washing Bay. Contractor was reminded to remove the water regularly especially after raining.</li> </ul>	B 15
	<b>C. Air Quality</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>D. Waste / Chemical Management</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>E. Waste / Chemical Management</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>F. Landscape</b>	
00609-R(1)	<ul style="list-style-type: none"> <li>To erect protection fence surrounding the remaining retaining trees.</li> </ul>	F 1
00609-R(2)	<ul style="list-style-type: none"> <li>Removal of protection fence is observed. Contractor was reminded to maintain the fence surrounding the retaining trees.</li> </ul>	F 4
	<b>G. Permits/Licences</b>	
	<ul style="list-style-type: none"> <li>No environmental deficiency was identified during site inspection.</li> </ul>	
	<b>H. Others</b>	
	<ul style="list-style-type: none"> <li>Environmental deficiencies were not rectified/improved by the Contractor during the site inspection: item 00602-R(1) and 00602-R(2) is remarked as item 00609-R(1) and 00609-O(1)</li> </ul>	

Contract No. SS W317

Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point

Weekly Site Inspection Record Summary

	Name	Signature	Date
Recorded by	Gary Lau		10 June 2010
Checked by	Dr. Priscilla Choy		10 June 2010



Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	00615
Date	15 June 2010 (Wednesday)
Time	14:30-16:30

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>B. Water Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>C. Air Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>D. Noise</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>E. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Landscape</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>G. Permits/Licences</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>H. Others</b>	
	• No environmental deficiency was identified during site inspection.	

	Reminders	Related Item No.
	The Contractor was reminded to implement the following preventive measures:	
	<b>B. Water Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>C. Air Quality</b>	
00615-R(3)	• Mud trail was observed near the wheels washing bay at gate No. 40. Contractor was reminded to clear it regularly.	C 2
	<b>D. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>E. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Landscape</b>	
00615-R(1)	• To erect protection fence surrounding the remaining retaining trees.	F 1
00615-R(2)	• Removal of protection fence is observed. Contractor was reminded to maintain the fence surrounding the retaining trees.	F 4
	<b>G. Permits/Licences</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>H. Others</b>	
	• Environmental deficiencies were not rectified/improved by the Contractor during the site inspection: item 00609-R(1) and 00609-R(2) is remarked as item 00615-R(1) and 00615-R(2)	

Contract No. SS W317

Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point

Weekly Site Inspection Record Summary

	Name	Signature	Date
Recorded by	Gary Lau	<i>Gary Lau</i>	17 June 2010
Checked by	Dr. Priscilla Choy	<i>Priscilla Choy</i>	17 June 2010

Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	00623
Date	23 June 2010 (Wednesday)
Time	14:30-16:30



Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>B. Water Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>C. Air Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>D. Noise</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>E. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Landscape</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>G. Permits/Licences</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>H. Others</b>	
	• No environmental deficiency was identified during site inspection.	

	Reminders	Related Item No.
	The Contractor was reminded to implement the following preventive measures:	
	<b>B. Water Quality</b>	
00623-R(2)	• To fill the wheels washing bay with sufficient water and desilting the water regularly.	B 16ii
00623-R(3)	• To cover the slope next to fish pond to prevent surface run-off occur during rainstorm.	B 11
	<b>C. Air Quality</b>	
00623-R(4)	• Exposed stockpile was observed next to gate No.34. Contractor was reminded to cover it with tarpaulin.	C 6
00623-R(5)	• Mud trail was observed at access road. Contractor was reminded to remove it regularly.	C 2
	<b>D. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>E. Waste / Chemical Management</b>	
00623-R(6)	• Chemical containers were observed without proper storage. Contractor was reminded to provide drip tray to contain them.	E 3iii
	<b>F. Landscape</b>	
00623-R(1)	• Removal of protection fence is observed. Contractor was reminded to erect and maintain the regularly.	F 4
	<b>G. Permits/Licences</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>H. Others</b>	
	• Environmental deficiencies were not rectified/improved by the Contractor during the site inspection: item 00615-R(1),R(2) and 00615-R(3) is remarked as item 00623-R(1) and 00623-R(5)	

Contract No. SS W317

Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point

Weekly Site Inspection Record Summary

	Name	Signature	Date
Recorded by	Gary Lau		25 June 2010
Checked by	Dr. Priscilla Choy		25 June 2010

Contract No. SS W317

Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point

Weekly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	00628
Date	28 June 2010 (Monday)
Time	15:00 – 16:00



Ref. No.	Non-Compliance	Related Item No.
-	None identified	-
Ref. No.	Remarks/Observations	Related Item No.
	<b>B. Water Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>C. Air Quality</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>D. Noise</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>E. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Landscape</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>G. Permits/Licences</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>H. Others</b>	
	• No environmental deficiency was identified during site inspection.	

	Reminders	Related Item No.
	The Contractor was reminded to implement the following preventive measures:	
	<b>B. Water Quality</b>	
00628-R(2)	• To cover the slope next to fish pond to prevent surface run-off occur during rainstorm.	B 11
	<b>C. Air Quality</b>	
00628-R(3)	• Exposed stockpile was observed next to gate No.34. Contractor was reminded to cover it with tarpaulin.	C 6
	<b>D. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>E. Waste / Chemical Management</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>F. Landscape</b>	
00628-R(1)	• To maintain the protection fencing around the retaining tree regularly.	F 4
00628-R(4)	• To remove the felled tree immediately after tree felling process to prevent damage made on retaining trees.	F 2
	<b>G. Permits/Licences</b>	
	• No environmental deficiency was identified during site inspection.	
	<b>H. Others</b>	
	• Environmental deficiencies were not rectified/improved by the Contractor during the site inspection: item 00623-R(3), 00623-R(4) are remarked as item 00628-R(2) and 00628-R(3)	

Contract No. SS W317

Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point

Weekly Site Inspection Record Summary

	Name	Signature	Date
Recorded by	Gary Lau		30 June 2010
Checked by	Dr. Priscilla Choy		30 June 2010

---

---

**APPENDIX F**  
**SUMMARY OF WASTE GENERATED**

---

---

**Appendix F - Waste Flow Table**

Name of Department : Architectural Services Department

Contract No. : SS W317

Programme No. : 15 GB

**Monthly Summary Waste Flow Table for 2010** (year) [to be submitted not later than the 15<sup>th</sup> day of each month following reporting month]

(All quantities shall be rounded off to 3 decimal places.)

Month	Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of C&D Wastes Generated Monthly				
	(a)=(b)+(c)+(d)+(e) Total Quantity Generated	(b) Broken Concrete (see Note 4)	(c) Reused in the Contract	(d) Reused in other Projects	(e) Disposed as Public Fill	(f) Metals	(g) Paper/ cardboard packaging	(h) Plastics (see Note 3)	(i) Chemical Waste	(j) Others, e.g. general refuse disposed at Landfill
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )
Jan	0	0	0	0	0	0	0	0	0	0
Feb	0	0	0	0	0	0	0	0	0	0
Mar	0	0	0	0	0	0	0	0	0	0
Apr	0	0	0	0	0	0	0	0	0	0.006
May	0	0	0	0	0	0	0	0	0	0
June	0	0	0	0	0	0	0	0	0	0.6
Sub-total	0	0	0	0	0	0	0	0	0	0.066
July										
Aug										
Sept										
Oct										
Nov										
Dec										
Total										

- Notes: (1) The performance targets are given in the Particular Specification on Waste Management Plan, Sub-clause 2(5)(c).  
 (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.  
 (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.  
 (4) Broken concrete for recycling into aggregates.  
 (5) If necessary, use the conversion factor: 1 full load of dumping truck being equivalent to 6.5 m<sup>3</sup> by volume.



**APPENDIX G  
ENVIRONMENTAL MITIGATION  
IMPLEMENTATION SCHEDULE (EMIS)**

## Appendix G - Environmental Mitigation Implementation Schedule (EMIS)

Types of Impacts	Mitigation Measures	Status
Air Quality	<i>Construction Phase</i>	
	<ul style="list-style-type: none"> <li>Excavated dusty materials or stockpile of dusty materials should be covered entirely by impervious sheeting or sprayed with water so as to maintain the entire surface wet, and recovered or backfilled or reinstated within 24 hours of the excavation or unloading.</li> </ul>	#
	<ul style="list-style-type: none"> <li>The working area of excavation should be sprayed with water immediately before, during and immediately after the operations so as to maintain the entire surface wet.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Vehicle washing area and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.</li> </ul>	N/A
	<ul style="list-style-type: none"> <li>The portion of road within 30m of designated vehicle entrance or exit should be kept clear of dusty materials.</li> </ul>	*
	<ul style="list-style-type: none"> <li>All dusty materials should be sprayed with water prior to any loading, unloading or transfer.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Vehicle speed should be limited to 10kph except on completed access roads.</li> </ul>	^
Noise	<ul style="list-style-type: none"> <li>Vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites.</li> </ul>	^
	<i>Construction Phase</i>	
	<ul style="list-style-type: none"> <li>Adopt the Code of Practice on Good Management Practice to comply with the Noise Control Ordinance (Chapter 400) (for Construction Industry) published by EPD</li> </ul>	^
	<ul style="list-style-type: none"> <li>Observe and comply with the statutory and non-statutory requirements and guidelines.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Before commencing any work, the Contractor shall submit to the Engineer Representative for approval the method of working, equipment and noise mitigation measures intended to be used at the site.</li> </ul>	^
	<ul style="list-style-type: none"> <li>The Contractor shall devise and execute working methods to minimise the noise impact on the surrounding sensitive uses, and provide experienced personnel with suitable training to ensure that those methods are implemented.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Noisy equipment and noisy activities should be located as far away from the NSRs as is practical.</li> </ul>	^
<ul style="list-style-type: none"> <li>Unused equipment should be turned off. PME should be kept to a minimum and the parallel use of noisy equipment / machinery should be avoided.</li> </ul>	^	
<ul style="list-style-type: none"> <li>Regular maintenance of all plant and equipment.</li> </ul>	^	

	<ul style="list-style-type: none"> <li>Material stockpiles and other structures should be effectively utilised as noise barriers, where practicable.</li> </ul>	^
	<i>Use of Quiet Plant and Movable Noise Barrier</i>	
	<ul style="list-style-type: none"> <li>Purpose-built movable noise barriers should be used to mitigate construction noise directly at sources that are not usually mobile provide that the direct line of sight to the source is blocked.</li> </ul>	N/A
<b>Water Quality</b>	<i>Construction Phase</i>	
	<ul style="list-style-type: none"> <li>The site should be confined to avoid silt runoff to the site.</li> </ul>	*
	<ul style="list-style-type: none"> <li>No discharge of silty water into the storm drain and drainage channel within and the vicinity of the site.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Stockpiles to be covered by tarpaulin to avoid spreading of materials during rainstorms;</li> </ul>	#
	<ul style="list-style-type: none"> <li>Suitable containers shall be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Chemical waste containers shall be labelled with appropriate warning signs in English and Chinese to avoid accidents. There shall also be clear instructions showing what action to take in the event of an accidental.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Storage areas shall be selected at safe locations on site and adequate space shall be allocated to the storage area.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Any construction plant which causes pollution to the water system due to leakage of oil or fuel shall be removed off-site immediately.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Spillage or leakage of chemical waste to be controlled by using suitable absorbent materials.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Chemicals will always be stored on drip trays or in bunded areas where the volume is 110% of the stored volume.</li> </ul>	*
	<ul style="list-style-type: none"> <li>Regular clearance of domestic waste generated in the temporary sanitary facilities to avoid waste water spillage.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Temporary sanitary facilities to be provided for on-site workers during construction</li> </ul>	^
	<i>Concreting Work</i>	
	<ul style="list-style-type: none"> <li>Set up a temporary drainage channel to collect the runoff generated and prevent concrete-contaminated water from entering watercourses. Adjustment of pH can be achieved by adding a suitable neutralising reagent to wastewater prior to discharge.</li> </ul>	^
	<i>Soil Excavation and Stockpiling</i>	
<ul style="list-style-type: none"> <li>Temporarily stockpiled excavated soil should be stored in a designated area and provided with a tarpaulin cover to avoid runoff into the drainage channels.</li> </ul>	#	
<i>Site Depot</i>		

	<ul style="list-style-type: none"> <li>All compounds in works areas should be located on areas of hard standing with provision of drainage channels and settlement ponds to allow interception and controlled release of settled/treated water.</li> </ul>	N/A
	<ul style="list-style-type: none"> <li>Hard standing compounds should drain via an oil interceptor, it should be regularly inspected and cleaned to avoid wash-out of oil during storm conditions. A bypass should be provided to avoid overload of the interceptor's capacity.</li> </ul>	N/A
	<ul style="list-style-type: none"> <li>Registered as a chemical waste producer for contractor generating waste oil or other chemicals. Disposal of the waste oil should be done by a licensed collector</li> </ul>	^
	<ul style="list-style-type: none"> <li>Appropriate training including safety codes and relevant manuals should be given to the personnel who regularly handle the chemicals on site to keep the storage and the work space in a tidy and clean condition.</li> </ul>	N/A
	<i>Construction of Checkpoint</i>	
	<ul style="list-style-type: none"> <li>Sewage system should be constructed to divert domestic sewage, which will be generated from the sanitary facilities provided in the new checkpoint at Shek Chung Au, to public sewer connected to government sewage treatment facilities.</li> </ul>	N/A
<b>Waste Management</b>	<i>Site Clearance</i>	
	<ul style="list-style-type: none"> <li>The topsoil and vegetation removed and excavated material may have to be temporarily stockpiled on-site to prevent the generation of dust and pollution of stormwater channels, fish ponds or river channels. Stockpiling of excavated materials during the wet season should be avoided as far as practicable.</li> </ul>	^
	<i>Construction Phase</i>	
	<ul style="list-style-type: none"> <li>Good site management to minimize over-ordering and generation of waste materials such as concrete mortars and cement grouts.</li> </ul>	^
	<ul style="list-style-type: none"> <li>The Contractor should recycle as much of the C&amp;D materials as possible on-site.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Trip-ticket system should be employed to monitor the disposal of C&amp;D material and solid at public filling facilities and landfills, and to control fly-tipping.</li> </ul>	^
	<i>Chemical Waste</i>	
	<ul style="list-style-type: none"> <li>To reduce generating chemical waste as much as possible.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Containers used for the storage of chemical wastes should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed, have a capacity of less than 450 litres with label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations.</li> </ul>	^
	<ul style="list-style-type: none"> <li>The storage area for chemical wastes should be clearly labelled and used solely for the storage of chemical waste.</li> </ul>	^
	<ul style="list-style-type: none"> <li>The storage area should be enclosed on at least 3 sides, have adequate ventilation with impermeable floor, capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Rainfall entering should be avoided entering to storage area and adequately separated with incompatible materials.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Disposal of chemical waste should be via a licensed waste collector to licensed facility which can supply the necessary storage containers, or to be re-user of the waste, under approval from the EPD.</li> </ul>	^
<i>General Refuse</i>		

	<ul style="list-style-type: none"> <li>Should be stored in enclosed bins or compaction units separate from C&amp;D and chemical wastes. The Contractor should employ a reputable waste collector to remove general refuse from the site, separate from C&amp;D and chemical wastes, on a regular basis to minimise odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Prohibition of refuse burning on construction sites</li> </ul>	^
	<i>Construction Waste Management Plan</i>	
	<ul style="list-style-type: none"> <li>Construction waste management plan (CWMP) should be prepared</li> </ul>	^
	<ul style="list-style-type: none"> <li>Contractor should ensure proper collection, treatment and disposal of waste on site.</li> </ul>	^
<b>Ecology</b>	<i>Ecological Impacts on Floral Species of Conservation Concern</i>	
	<ul style="list-style-type: none"> <li>Erection of protective fencing to protect the plant during construction period</li> </ul>	*
	<i>Potential Ecological Impacts on Offsite Habitats</i>	
	<ul style="list-style-type: none"> <li>Controlling the dust and water quality by avoiding stockpiles adjacent to wetlands and covering the stockpiles with impervious sheeting.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Controlling vehicle speed and ensure no discharge of silty water to the rivers, streams.</li> </ul>	^
	<i>Disturbance to Wetland-Dependent Birds, Raptors, Terrestrial Birds and Egretty</i>	
	<ul style="list-style-type: none"> <li>Restriction of excavation works within a 150m buffer zone from the egretty to ardeid non-breeding season (from August to February).</li> </ul>	^
	<ul style="list-style-type: none"> <li>Switching off unused equipment, keep minimum number of powered mechanical equipment in operation at the same period, the use of stockpiles and other structures to form noise barriers where practicable to avoid causing disturbance to feeding the wildlife.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Proper cover of stockpiles with impervious sheeting to minimize construction noise, uncontrolled surface runoff and discharge of silts.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Avoidance of construction works using Power Mechanical Equipments within the Wetland Conservation Area during bird migratory season (15th November – 15th March).</li> </ul>	^
<b>Landscape and Visual</b>	<i>Preservation of Existing Vegetation throughout construction phase</i>	
	<ul style="list-style-type: none"> <li>To retain trees that have high amenity or ecology value and contribute most to the landscape and visual amenity of the site and its immediate environs.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Prohibition of the storage of materials including fuel, the movement of construction vehicles, and the refuelling and washing of equipment including concrete mixers within the precautionary area</li> </ul>	^
	<ul style="list-style-type: none"> <li>Phased segmental root pruning for trees to be retained over a suitable period (determined by species and size) prior to lifting or site formation works which affect the existing rootball of trees identified for retention. The extent of the pruning will be based on the size and the species of the tree in each case.</li> </ul>	^
	<ul style="list-style-type: none"> <li>Pruning of the branches of existing trees identified for retention to be based on the principle of crown thinning maintaining their form and amenity value.</li> </ul>	^
	<ul style="list-style-type: none"> <li>The watering of existing vegetation particularly during periods of excavation when the water table beneath the existing vegetation is lowered.</li> </ul>	^
	<ul style="list-style-type: none"> <li>The rectification and repair of damaged vegetation following the construction phase to its original condition prior to the commencement of the works or replacement using specimens of the same species, size and form</li> </ul>	^

	where appropriate to the design intention of the area affected	
	<ul style="list-style-type: none"> <li>All works affecting the trees identified for retention will be carefully monitored, including the key stages in the preparation of the trees, the implementation of protection measures and health monitoring through out the construction period</li> </ul>	^
	<ul style="list-style-type: none"> <li>Detailed landscape and tree preservation proposals will be submitted to the relevant government departments for approval under the lease conditions and in accordance with ETWB TCW No. 2/2004 and WBTC No. 3/2006.</li> </ul>	^
	<ul style="list-style-type: none"> <li>The tree preservation works should be implemented by approved Landscape Contractors and inspected and approved on site by a qualified Landscape Architect. A tree protection specification would be included within the contract documents.</li> </ul>	^
<i>Preservation of Existing Topsoil</i>		
	<ul style="list-style-type: none"> <li>Topsoil disturbed during the construction phase should be tested using a standard soil testing methodology and where it is found to be worthy of retention stored for re-use.</li> </ul>	N/A
	<ul style="list-style-type: none"> <li>The soil will be stockpiled to a maximum height of 2m and will be either temporarily vegetated with hydroseeded grass during construction or covered with a waterproof covering to prevent erosion.</li> </ul>	N/A
	<ul style="list-style-type: none"> <li>Regularly turned over the stockpile to avoid acidification and the degradation of the organic material, and reused after completion.</li> </ul>	N/A
	<ul style="list-style-type: none"> <li>Considered for re-use in other projects when above actions are not practical.</li> </ul>	N/A
<i>Permanent and Temporary Works Areas</i>		
	<ul style="list-style-type: none"> <li>Where appropriate to the final design the landscape of these works areas should be restored following the completion of the construction phase.</li> </ul>	N/A
	<ul style="list-style-type: none"> <li>Construction site controls should be enforced including the storage of materials, the location and appearance of site accommodation and the careful design of site lighting to prevent light spillage.</li> </ul>	^
<i>Mitigation Planting</i>		
	<ul style="list-style-type: none"> <li>Replanting of disturbed vegetation should be undertaken at the earliest possible stage of the construction phase</li> </ul>	N/A
	<ul style="list-style-type: none"> <li>Use of native plant species predominantly in the planting design for the buffer areas.</li> </ul>	N/A

Remarks:	^	Compliance of mitigation measure;
	N/A	Not Applicable;
	*	Recommendation was made during site audit but improved/rectified by the contractor.
	#	Recommendation was made during site audit but not yet improved/rectified by the contractor in reporting month.
	X	Non-compliance of mitigation measure;
	•	Non-compliance but rectified by the contractor;

---

---

**APPENDIX H  
EVENT ACTION PLANS FOR  
CONSTRUCTION NOISE**

---

---

**Appendix H- Event and Action Plan for Construction Noise**

EXCEEDANCE	ACTION			
	ET	IEC	Engineer	Contractor
<b>Action Level</b>	1. Notify IEC and the HKKT. 2. Carry out investigation. 3. Report the results of investigation to IEC and the HKKT. 4. Discuss with the HKKT and formulate remedial measures. 5. Increase monitoring frequency to check mitigation measures.	1. Review with analyzed results submitted by ET. 2. Review the proposed remedial measures by the HKKT and advise ER accordingly. 3. Supervise the implement of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the HKKT. 3. Require the HKKT to propose remedial measures for the analyzed noise problem. 4. Ensure remedial measures are properly implemented.	1. Submit noise mitigation proposals to IEC. 2. Implement noise mitigation proposals.
<b>Limit Level</b>	1. Identify the source. 2. Notify IEC, ER, EPD and the HKKT. 3. Repeat measurement to confirm findings. 4. Increase monitoring frequency. 5. Carry out analysis of HKKT's working procedures to determine possible mitigation to be implemented. 6. Inform IEC, ER, and EPD the causes & actions taken for the exceedances. 7. Assess effectiveness of the HKKT's remedial actions and keep IEC, EPD and ER informed of the results. 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET Leader and the HKKT on the potential remedial actions. 2. Review the HKKT's remedial actions whenever necessary to assure their effectiveness and advise ER accordingly. 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of exceedance in writing. 2. Notify the HKKT. 3. Require the HKKT to propose remedial measures for the analyzed noise problem. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what activity of the work is responsible and instruct the HKKT to stop that activity of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problem still not under control. 5. Stop the relevant activity of works as determined by the ER until the exceedance is abated.



---

---

**APPENDIX I  
TENTATIVE CONSTRUCTION  
PROGRAMME**

---

---









2010年12月	2011年1月	2011年2月	2011年3月	2011年4月	2011年5月	2011年6月	2011年7月	2011年8月	2011年9月	2011年10月	2011年11月	2011年12月	2012年1月	2012年2月	2012年3月	2012年4月	2012			
8/1 5/12 2/1 9/1 6/1	2/1 9/1 16/1 23/1 30/1	6/2 13/2 20/2 27/2	6/3 13/3 20/3 27/3	3/4 10/4 17/4 24/4	1/5 8/5 15/5 22/5 29/5	5/6 12/6 19/6 26/6	3/7 10/7 17/7 24/7	31/7 7/8 14/8 21/8 28/8	4/9 11/9 18/9 25/9	2/10 9/10 16/10 23/10	3/1 0/1 6/11 13/1 20/1	7/1 4/12 1/1 8/1 5/1	1/1 8/1 15/1 22/1 29/1	5/2 12/2 19/2 26/2	4/3 11/3 18/3 25/3	1/4 8/4 15/4 22/4	29/4 6/5			

2010年12月	2011年1月	2011年2月	2011年3月	2011年4月	2011年5月	2011年6月	2011年7月	2011年8月	2011年9月	2011年10月	2011年11月	2011年12月	2012年1月	2012年2月	2012年3月	2012年4月	2012			
8/1 5/12 2/1 9/1 6/1	2/1 9/1 16/1 23/1 30/1	6/2 13/2 20/2 27/2	6/3 13/3 20/3 27/3	3/4 10/4 17/4 24/4	1/5 8/5 15/5 22/5 29/5	5/6 12/6 19/6 26/6	3/7 10/7 17/7 24/7	31/7 7/8 14/8 21/8 28/8	4/9 11/9 18/9 25/9	2/10 9/10 16/10 23/10	3/1 0/1 6/1 13/1 20/1	7/1 4/12 1/1 8/1 5/1	1/1 8/1 15/1 22/1 29/1	5/2 12/2 19/2 26/2	4/3 11/3 18/3 25/3	1/4 8/4 15/4 22/4 29/4	6/5			

---

---

**APPENDIX J  
ENVIRONMENTAL MONITORING  
SCHEDULE S**

---

---



**Contract No. SS W317 Impact Noise Monitoring for  
Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point  
Noise Monitoring Schedule for June 2010**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-Jun	2-Jun	3-Jun	4-Jun	5-Jun
		Noise				
<b>6-Jun</b>	7-Jun	8-Jun	9-Jun	10-Jun	11-Jun	12-Jun
			Noise			
<b>13-Jun</b>	14-Jun	15-Jun	<b>16-Jun</b>	17-Jun	18-Jun	19-Jun
		Noise				
<b>20-Jun</b>	21-Jun	22-Jun	23-Jun	24-Jun	25-Jun	26-Jun
		Noise				
<b>27-Jun</b>	28-Jun	29-Jun	30-Jun			
		Noise				

**Noise Monitoring Station**

VH01 - Village House at Mai Po

VH03 - Village House at Mai Po

**Contract No. SS W317 Impact Noise Monitoring for  
Construction of a Secondary Boundary Fence from Mai Po to Lok Ma Chau Control Point  
Tentative Noise Monitoring Schedule for July 2010**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				<b>1-Jul</b>	2-Jul	3-Jul
<b>4-Jul</b>	5-Jul	6-Jul	7-Jul	8-Jul	9-Jul	10-Jul
		Noise				
<b>11-Jul</b>	12-Jul	13-Jul	14-Jul	15-Jul	16-Jul	17-Jul
		Noise				
<b>18-Jul</b>	19-Jul	20-Jul	21-Jul	22-Jul	23-Jul	24-Jul
		Noise				
<b>25-Jul</b>	26-Jul	27-Jul	28-Jul	29-Jul	30-Jul	31-Jul
		Noise				

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)

**Noise Monitoring Station**

VH01 - Village House at Mai Po

VH03 - Village House at Mai Po
