

JOB NO.: TCS00757/15

DSD CONTRACT NO. DC/2013/09 – Advance Works for Shek Wu Hui Sewage Treatment Works – Further Expansion Phase 1A and Sewerage Works at Ping Che Road

11th Monthly Environmental Monitoring and Audit (EM&A) Report – August 2016

PREPARED FOR TSUN YIP WATERWORKS CONSTRUCTION CO LTD

Date	Reference No.	Prepared By	Certified By
13 September 2016	TCS00757/15/600/R0054v2	Att	Am

Martin Li (Assistant Environmental Consultant)

Tam Tak Wing (Environmental Team Leader)

Version	Date	Remarks
1	9 September 2016	First Submission
2	13 September 2016	Amended against IEC's comment



Drainage Services Department 44/F., Revenue Tower 5 Gloucester Road Wan Chai Hong Kong Your reference:

Our reference:

HKDSD201/50/103748

Date: 13 Septe

13 September 2016

Attention: Mr Michael Leung

BY EMAIL & POST (email: hkleung@dsd.gov.hk)

Dear Sirs

Agreement No.: SP 01/2015 Environmental Monitoring and Audit for Advance Works for Shek Wu Hui Sewage Treatment Works – Further Expansion Phase 1A Monthly EM&A Report for August 2016

We refer to emails of 9 and 13 September 2016 attaching a Monthly EM&A Report for August 2016 for the captioned project prepared by the Environmental Team (ET) of the captioned project.

We have no further comment and hereby verify the Monthly EM&A Report in accordance with Clause 3.4 of the Environmental Permit no. FEP-01/474/2013.

Please do not hesitate to contact the undersigned at 2618 2836 should you have any queries.

Yours faithfully ANEWR CONSULTING LIMITED

Adu Lee Independent Environmental Checker

LYMA/csym

cc Tsun Yip – Mr Ken Wong (email: kenwong@tsunyip.hk) AUES – Ms Nicola Hon (email: nicolahon@fordbusiness.com)







EXECUTIVE SUMMARY

ES.01 This is the 11th Monthly Environmental Monitoring and Audit Report covering the period from 1 to 31 August 2016 (the Reporting Period).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES.02 Environmental monitoring activities under the EM&A program in this Reporting Period are summarized in the following table.

Issues	Environmental Monitoring Parameters / Inspection	Occasions
Air Quality	1-hour TSP	36
All Quality	24-hour TSP	10
Construction Noise	L _{Aeq(30min)} Daytime	10
Inspection / Audit	ET Regular Environmental Site Inspection	5
Inspection / Audit	IEC Monthly Environmental Site Audit	1

BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES.03 No exceedance of air quality and construction noise monitoring were recorded in this Reporting Period. No Notification of Exceedance (NOE) was therefore issued. The statistics of environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

Environmental	Monitoring Action		Limit	Event & Action		
Issues	Parameters	Level	Level	NOE Issued	Investigation	Corrective Actions
Air Quality	1-hour TSP	0	0	0	-	-
All Quality	24-hour TSP	0	0	0	-	-
Construction Noise	LAeq(30min)	0	0	0	-	-

Note: NOE – Notification of Exceedance

ENVIRONMENTAL COMPLAINT

ES.04 No environmental complaint was recorded or received in this Reporting Period. The statistics of environmental complaint are summarized in the following table.

Depenting Devied	Environmental Complaint Statistics			
Reporting Period	Frequency	Cumulative	Complaint Nature	
1 to 31 August 2016	0	0	NA	

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES.05 No environmental summons or successful prosecutions were recorded in this Reporting Period. The statistics of environmental complaint are summarized in the following tables.

Departing Deviad	Environmental Summons Statistics			
Reporting Period	Frequency	Cumulative	Complaint Nature	
1 to 31 August 2016	0	0	NA	

Poporting Poriod	Environmental Prosecution Statistics			
Reporting Period	Frequency	Cumulative	Complaint Nature	
1 to 31 August 2016	0	0	NA	

REPORTING CHANGE

ES.06 There were no reporting changes in the Reporting Period.

SITE INSPECTION BY EXTERNAL PARTIES

ES.07 In the Reporting Period, joint site inspection to evaluate the site environmental performance by the RE, ET and the Contractor was carried out on 4, 9, 16, 23 and 30 August 2016. Furthermore, IEC attend site inspection was on 30 August 2016. No non-compliance was noted.



FUTURE KEY ISSUES

- ES.08 As wet season is approached, special attention should be paid to avoid ingress of surface runoff into nearby water bodies from the construction site. Water quality mitigation measures should be fully implemented.
- ES.09 Air quality mitigation measures including wheel wash facilities, watering of haul roads and covering of dusty materials with tarpaulin sheet, etc. should be properly maintained. Moreover, the contractor should be to prevent mosquito breeding on site.



Table of Contents

1	INTRODUCTIO	ON	1
	1.1 Proj	ECT BACKGROUND	1
	1.2 REPO	RT STRUCTURE	2
2	PROJECT ORG	GANIZATION AND CONSTRUCTION PROGRESS	3
		ECT ORGANIZATION AND MANAGEMENT STRUCTURE	3
	2.2 Cons	TRUCTION PROGRESS	3
	2.3 SUMM	MARY OF ENVIRONMENTAL SUBMISSIONS	3
3	SUMMARY OF	IMPACT MONITORING REQUIREMENT	4
C	3.1 GENE		4
	3.2 MON	ITORING PARAMETERS	4
		ITORING LOCATIONS	4
	3.4 Mon	ITORING FREQUENCY AND PERIOD	4
	3.5 MON	ITORING EQUIPMENT	5
	3.6 Dete	RMINATION OF ACTION/LIMIT (A/L) LEVELS	6
	3.7 EVEN	IT ACTION PLAN	6
4	MONITORING	METHDOLOGY	7
		QUALITY MONITORING	7
	4.2 Cons	TRUCTION NOISE MONITORING	7
	4.3 DATA	MANAGEMENT AND DATA QA/QC CONTROL	8
5	IMPACT MON	ITORING RESULTS	9
	5.1 GENE		9
	5.2 Resu	LTS OF AIR QUALITY MONITORING	9
	5.3 Resu	LTS OF CONSTRUCTION NOISE MONITORING	10
6	WASTE MANA	GEMENT	11
Ū		ERAL WASTE MANAGEMENT	11
		ORDS OF WASTE QUANTITIES	11
7	SITE INSPECT	ION	12
'		JIREMENTS	12
	· · · · ·	INGS / DEFICIENCIES DURING THE REPORTING MONTH	12
8	FNVIRONMEN	NTAL COMPLAINT AND NON-COMPLIANCE	13
0		RONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	13
9		TION STATUS OF MITIGATION MEASURES	14
,		ERAL REQUIREMENTS	14
		ATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH	14
		Issues for the Coming Month	14
10		S AND RECOMMENTATIONS	
10		S AND RECOMMENTATIONS CLUSIONS	16 16
		DIMMENDATIONS	16
	10.2 RECC		10



LIST OF TABLES

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	PROPOSED AIR QUALITY AND CONSTRUCTION NOISE MONITORING LOCATIONS
TABLE 3-3	AIR QUALITY MONITORING EQUIPMENT
TABLE 3-4	CONSTRUCTION NOISE MONITORING EQUIPMENT
TABLE 3-5	Action and Limit Levels for 24-Hr TSP and 1-Hr TSP Air Quality, $\mu g/m^3$
TABLE 3-6	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 5-1	SUMMARY OF 1-HOUR TSP MONITORING RESULTS, $\mu g/m^3$
TABLE 5-2	SUMMARY OF 24-HOUR TSP MONITORING RESULTS, $\mu g/m^3$
TABLE 5-3	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS, dB(A)
TABLE 6-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS FOR THE PROJECT
TABLE 6-2	SUMMARY OF QUANTITIES OF C&D WASTES FOR THE PROJECT
TABLE 7-1	SITE OBSERVATIONS
TABLE 8-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 8-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 8-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 9-1	ENVIRONMENTAL MITIGATION MEASURES

LIST OF APPENDICES

APPENDIX A	GENERAL LAYOUT OF ADVANCE WORKS AND MAIN WORKS OF SWHSTW FURTHER EXPANSION PHASE 1A		
APPENDIX B	LAYOUT PLAN OF THE CONTRACT		
APPENDIX C	ORGANIZATION STRUCTURE AND CONTACT DETAILS OF RELEVANT PARTIES		
APPENDIX D	MASTER CONSTRUCTION PROGRAM OF THE CONTRACT		
APPENDIX E	PROPOSED MONITORING LOCATIONS		
APPENDIX F	EVENT ACTION PLAN		
APPENDIX G	VALID CALIBRATION CERTIFICATES		
APPENDIX H	IMPACT MONITORING SCHEDULE		
APPENDIX I	24-HOUR TSP AND CONSTRUCTION NOISE MONITORING DATA		
APPENDIX J	GRAPHICAL PLOTS		
APPENDIX K	METEOROLOGICAL DATA DURING THE REPORTING MONTH		
APPENDIX L	MONTHLY SUMMARY WASTE FLOW TABLE		
APPENDIX M	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)		



1 INTRODUCTION

1.1 PROJECT BACKGROUND

- 1.1.1 The existing Shek Wu Hui Sewage Treatment Works (hereafter referred as "SWHSTW") with secondary level treatment to sewage collected from Sheung Shui, Fanling and adjacent areas is operated and maintained by Drainage Services Department (hereafter referred as "DSD"). Based on the preliminary design of the Project, the scope of works for the Project comprises the following major components:
 - (a) Demolition of the existing Inlet Works and construction of the new Inlet Works, including inlet pumping station, screening and degritting facilities;
 - (b) Demolition of 4 existing circular Primary Sedimentation Tanks (PSTs) and construction of new rectangular PSTs;
 - (c) Construction of new pre-membrane screens;
 - (d) Modification of existing Bioreactor (BR) 1 and 2 to suit the proposed membrane bioreactor (MBR) process;
 - (e) Construction of a new standby Bioreactor;
 - (f) Demolition of 4 existing circular Final Sedimentation Tanks (FSTs) and construction of new Membrane Tanks and Membrane Facility Building;
 - (g) Reconstruction of sludge treatment facilities, including thickening, anaerobic digestion, biogas handling, sludge holding and dewatering facilities; and
 - (h) Other ancillary works.
- 1.1.2 According to the Project implementation programme, the construction of most of the above proposed works (hereinafter referred to as "Main Works") will be commencement in 2016 and completion in 2022. Furthermore, Advance Works as part of the above proposed works will carry out before Main Works commencement. The Advance Works will be commencement in third quarter of 2015 and comprise the following major components:
 - (a) Modification of BR1, through upgrading of electrical and mechanical (E&M) equipment and minor civil works, to suit the proposed MBR process;
 - (b) Demolition of FSTs 1 and 2 and construction of Membrane Tanks and the first phase of Membrane Facility Building; and
 - (c) Tree felling and transplanting, to facilitate timely construction of the new Inlet Works during the implementation of Main Works (under review).
- 1.1.3 The general layout of Advance Works and Main Works of SWHSTW Further Expansion Phase 1A show in *Appendix A*. Subsequent to Further Expansion Phase 1A, the SWHSTW will be further expanded under separate projects (namely Further Expansion Phase 1B and Phase 2).
- 1.1.4 In July 2015, Tsun Yip Waterworks Construction Co Ltd (hereinafter referred as "Tsun Yip" or "the Contractor") has awarded the DSD Contract No. DC/2013/09 Advance Works for Shek Wu Hui Sewage Treatment Works Further Expansion Phase 1A and Sewerage Works at Ping Che Road (hereinafter referred as "the Contract"). The Contract is the Advance Works for Shek Wu Hui Sewage Treatment Works as part of SWHSTW Further Expansion which is a Designated Project under Environmental Permit number FEP-01/474/2013 (hereinafter referred as "the FEP-01/474/2013" or "the EP").
- 1.1.5 The works under the Contract at Shek Wu Hui Sewage Treatment Works will be included the conversion of one existing bioreactor and two existing final sedimentation tanks into one membrane bioreactor. Moreover, construction of about 1.5 kilometres length of sewers at Ping Che Road and other ancillary works will be undertaken. The works of Contract are scheduled to be conduct about 25 months. Layout plan of the Contract is shown in *Appendix B*.
- 1.1.6 Action-United Environmental Services & Consulting (hereinafter referred as "AUES") was appointed by the Contractor as an Environmental Team (hereinafter referred as "the ET") to



implement the relevant EM&A program in accordance with the Updated EM&A Manual, as well as the associated duties.

- 1.1.7 As part of the EM&A program, baseline monitoring is required to determine the ambient environmental conditions. Hence baseline monitoring including air quality and noise were carried out between 28 August 2015 and 12 September 2015 at the proposed locations before construction work commencement. The "Baseline Monitoring Report (TCS00757/15/600/R0014 Version 2)" had submitted to EPD by the DSD before commencement of major construction works and approved by the IEC on 24 September 2015. Further to Tsun Yip's instructions, the EM&A program was commenced on 1 October 2015 and the monitoring schedule had been issued to relevant parties on 29 September 2015.
- 1.1.8 This is the **11th** Monthly EM&A Report presenting the monitoring results and inspection findings for the reporting period from **1** to **31** August 2016.

1.2 REPORT STRUCTURE

1.2.1 The Monthly Environmental Monitoring and Audit (EM&A) Report is structured into the following sections:-

Section 1	INTRODUCTION
Section 2	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS
Section 3	SUMMARY OF MONITORING REQUIREMENTS
Section 4	IMPACT MONITORING RESULTS
Section 5	WASTE MANAGEMENT
Section 6	SITE INSPECTIONS
Section 7	Environmental Complaints and Non-Compliance
Section 8	IMPLEMENTATION STATUES OF MITIGATION MEASURES
Section 9	Impact Forecast
Section 10	CONCLUSIONS AND RECOMMENDATION



2 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

2.1 PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE

2.1.1 Organization structure and contact details of relevant parties with respect to on-site environmental management are shown in *Appendix C*.

2.2 CONSTRUCTION PROGRESS

- 2.1.2 Master Construction Program of the Contract is enclosed in *Appendix D* and the major construction activities undertaken in this Reporting Month are illustrated in *Appendix B* and listed below:-
 - Welding for Pile Head Steel Plate (At Membrane Facilities Building)
 - Erection of Formwork and Falsework (At Membrane Facilities Building)
 - Preparation of Re-bar Fixing Works (At Membrane Facilities Building)
 - Excavation and Installation of Sheet Pile for DN900 Trench (Near Final Sedimentation Tank No.5)
 - Restore BR2 and Suspend BR1 (At BR1 and BR2 Common Channel)
 - Deposition and Compaction of Coarse Aggregate on Carriageway (V.O.6, Near Control Room No.2)
 - Concreting the 100mm THK Wall on Carriageway (V.O.6, Near Control Room No.2)

2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.1.3 Summary of the relevant permits, licences, and/or notifications on environmental protection for this Project in this Reporting Period is presented in *Table 2-1*.

Item	Description	License/Permit Status
1	Air Pollution Control (Construction Dust) Regulation	Notified EPD on 30 July 2015
2	Chemical waste Producer Registration	Application date: 19/08/2015
	(WPN: 5213-624-T3148-04)	Date approved: 18/9/2015
3	Water Pollution Control Ordinance	Application date: 19/08/2015
	(Discharge License: WT00022503-2015)	Date approved: 18/9/2015
4	Billing Account for Disposal of Construction Waste	Granted on 02/09/2015
	(Account Number: 7022898)	

 Table 2-1
 Status of Environmental Licenses and Permits

- 2.1.4 In accordance with the Further EP No. FEP-01/474/2013 Condition 2.3, an Updated Environmental Monitoring and Audit (EM&A) Manual (TCS00757/15/600/R0012v3) which certified by the Environmental Team (ET) Leader and verified by the Independent Environmental Checker (IEC), has submitted to DSD and EPD endorsement.
- 2.1.5 Baseline Monitoring Report (TCS00757/15/600/R0014v2) as certified by the ETL and verified by the IEC was submitted to the EPD on 24 September 2015 for endorsement.



3 SUMMARY OF IMPACT MONITORING REQUIREMENT

3.1 GENERAL

- 3.1.1 The Environmental Monitoring and Audit requirements are set out in the Updated EM&A manual. Environmental issues such as air quality and construction noise were identified as the key issues during the construction phase of Advance Works of the Project.
- 3.1.2 A summary of EM&A programme of construction phase are presented in the sub-sections below.

3.2 MONITORING PARAMETERS

- 3.2.1 The EM&A programme of construction phase shall cover the following environmental issues:Air quality; and
 - Construction noise
- 3.2.2 A summary of the monitoring parameters is presented in *Table 3-1* below

Environmental Issue	Parameters
Air Quality	 1-hour TSP by Real-Time Portable Dust Meter; and 24-hour TSP by High Volume Air Sampler.
Construction Noise	 Leq_(30min) during normal working hours; and Leq_(15min) for the construction works undertaken in Restricted Hours, if necessary.

Table 3-1Summary of EM&A Requirements

3.3 MONITORING LOCATIONS

3.3.1 According to the *Updated EM&A Manual of* Advance Works which submitted to EPD on 25 *August 2015*, three air quality sensitive receivers and two construction noise sensitive receivers are proposed to monitor the environmental performance of the Contract. The proposed monitoring locations are summarized in *Table 3-2* and shown in *Appendix E*.

 Table 3-2
 Proposed Air Quality and Construction Noise Monitoring Locations

Aspect	Station ID	Location	Parameter
	AM1	No. 31 Wai Loi Tsuen	1- hour and 24- hour TSP
Air Quality	AM2	Fu Tei Au	1- hour
	AM2a	RE's Site Office	24- hour TSP
Noise	NM1	No. 31 Wai Loi Tsuen	Leq(30min)
noise	NM2	Fu Tei Au	L _{eq(30min)}

3.4 MONITORING FREQUENCY AND PERIOD

3.4.1 The requirements of baseline monitoring are stipulated in *Sections 2.1.7 and 3.2.5* of the Updated *EM&A Manual* and presented as follows.

Air Quality Monitoring

- 3.4.2 Monitoring frequency for air quality baseline monitoring is as follows:
 - 1-Hour TSP 3 sets of 1-hour TSP monitoring shall be carried out once in every six days.
 - 24-Hour TSP 24-hour shall be carried out once in every six days.

Noise Monitoring

3.4.3 Construction noise monitoring should be carried out at the designated monitoring station when there are Project-related construction activities being undertaken within a radius of 300m from the monitoring stations. The monitoring frequency should depend on the scale of the construction activities. An initial guide on the monitoring is to obtain one set of 30-minute



measurement at each station between 0700 and 1900 hours on normal weekdays at a frequency of once a week when construction activities are underway.

3.4.4 If construction works are extended to include works during the hours of 1900 - 0700, additional weekly impact monitoring shall be carried out during evening and night-time works. Applicable permits under NCO shall be obtained by the Contractor.

3.5 MONITORING EQUIPMENT

Air Quality Monitoring

- 3.5.1 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.* If the ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to the IEC to approve.
- 3.5.2 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.
- 3.5.3 All equipment as used air quality monitoring is listed in *Table 3-3*.

Table 3-3Air Quality Monitoring Equipment

Equipment	Model				
	24-Hr TSP				
High Volume Air Sampler	TISCH High Volume Air Sampler, HVS Model TE-5170				
Calibration Kit TISCH Model TE-5025A					
	1-Hour TSP				
Portable Dust Meter	Sibata LD-3 Laser Dust monitor Particle Mass Profiler &				
Portable Dust Meter	Counter				

Wind Data Monitoring Equipment

3.5.4 According to the Updated EM&A Manual Sections 2.1.3.8, alternative methods to obtain representative wind data was proposed by the ET. Meteorological information as extracted from "the Hong Kong Observatory Ta Kwu Ling Station" is alternative method to obtain representative wind data. For Ta Kwu Ling Station, it is located nearby the Project site. Moreover, this station is situated the sea level above 15mPD. The station's wind data monitoring equipment is set above the existing ground ten meters in compliance with the general setting up requirement. Furthermore, this station can also provide the humidity, rainfall, and air pressure and temperature etc. meteorological information. In a lot of Hong Kong development projects, weather information extracted from Hong Kong Observatory is a common alternative method if installation of weather station is not allowed.

Noise Monitoring

3.5.5 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m s⁻¹.

3.5.6 Noise monitoring equipment to be used for impact monitoring is listed in *Table 3-4*.

Table 3-4Construction Noise Monitoring Equipment

Equipment	Model
Integrating Sound Level Meter	Rion NL-52
Calibrator	Rion NC-73 / BK4231
Portable Wind Speed Indicator	Testo Anemometer

3.5.7 Sound level meters listed above comply with the International Electrotechnical Commission



Publications 651: 1979 (Type 1) and *804: 1985 (Type 1)* specifications, as recommended in TM issued under the NCO. The acoustic calibrator and sound level meter to be used in the baseline monitoring will be calibrated yearly.

3.6 DETERMINATION OF ACTION/LIMIT (A/L) LEVELS

3.6.1 According to the baseline monitoring results and the Updated EM&A Manual, the air quality and construction noise criteria were set up, namely Action and Limit levels are listed in *Tables* 3-5 & 3-6 as below.

Manitaning Stations	Action Le	evel (µg/m ³)	Limit Level (µg/m ³)		
Monitoring Stations	1-hour	24-hour	1-hour	24-hour	
AM1	286	147	500	260	
AM2	276	NA	500	NA	
AM2a	NA	155	NA	260	

Table 3-5 Action and Limit Levels for 24-Hr TSP and 1-Hr TSP Air Quality, µg m⁻³

Table 3-6	Action and Limit Levels for Construction Noise

Monitoring Stations	Action Level	Limit Level in dB(A)			
Time Period: 0700-1900 hours on normal weekdays					
NM1 and NM2	> 75* dB(A)				

Note: (*) Reduces to 70 dB(A) for schools and 65 dB(A) during the school examination periods.

3.7 EVENT ACTION PLAN

3.7.1 If non-compliance or exceedance of the Action/Limit Levels is occurred, actions shall be taken in accordance with the Event Action Plan in *Appendix F*.



4 MONITORING METHDOLOGY

4.1 **AIR QUALITY MONITORING**

Monitoring Location

4.1.1 The detailed information of air quality monitoring stations referred to *Table 3-2* and the graphical plot of monitoring locations shown in *Appendix E* in this report.

Monitoring Equipment

4.1.2 All the monitoring equipment to be used in the EM&A program as listed in *Table 3-3* has been agreed with the IEC.

Monitoring Procedures

1-hour TSP

- 4.1.3 The 1-hour TSP monitor, a Sibata LD-3 Laser Dust monitor Particle Mass Profiler & Counter was used for baseline monitoring, which is a portable, battery-operated laser photometer. The 1-hour TSP meter provides a real time 1-hour TSP measurement based on 90^o light scattering. The 1-hour TSP monitor consisted of the following:
 - a. A pump to draw sample aerosol through the optic chamber where TSP is measured;
 - b. A sheath air system to isolate the aerosol in the chamber to keep the optics clean for maximum reliability; and
 - c. A built-in data logger compatible with Windows based program to facilitate data collection, analysis and reporting.
- 4.1.4 The 1-hour TSP meter used is within the valid period, calibrated by the manufacturer prior to purchasing. Zero response of the instrument was checked before and after each monitoring event. Operation of the 1-hour TSP meter was follow manufacturer's Operation and Service Manual. A valid calibration certificate is attached in *Appendix G*.

24-hour TSP

- 4.1.5 The equipment used for 24-hour TSP measurement is a Tisch Environmental, Inc. Model TE-5170 TSP high volume air sampling system, which complied with EPA Code of Federal Regulation, Appendix B to Part 50. The High Volume Air Sampler (HVS) consists of the following:
 - a. An anodized aluminum shelter;
 - b. A 8"x10" stainless steel filter holder;
 - c. A blower motor assembly;
 - d. A continuous flow/pressure recorder;
 - e. A motor speed-voltage control/elapsed time indicator;
 - f. A 7-day mechanical timer, and
 - g. A power supply of 220v/50 hz
- 4.1.6 Prior to 24-hour TSP monitoring, the HVS was calibrated in accordance with the manufacturer's instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5028A). The 24-hour TSP Monitoring using the HVS was also processed in accordance with the manufacturer's Operations Manual. A valid calibration certificate of the calibration kit with the certificate of HVS calibrated is attached in *Appendix G*.
- 4.1.7 24-hour TSP was collected by the ET on filters of HVS and quantified by a local HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd (ALS), upon receipt of the samples. The ET keeps all the sampled 24-hour TSP filters in normal air conditioned room conditions, i.e. 70% HR (Relative Humidity) and 25°C, for six months prior to disposal.

4.2 CONSTRUCTION NOISE MONITORING



Monitoring Location

4.2.1 The detailed information of construction noise monitoring stations referred to *Table 3-2* and the graphical plot of monitoring locations shown in *Appendix E* in this report.

Monitoring Equipment

- 4.2.2 All the monitoring equipment to be used in the EM&A program as listed in *Table 3-3* has been agreed with the IEC.
- 4.2.3 Sound level meter listed in *Table 3-4* is complied with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications, as recommended in Technical Memorandum (TM) issued under the Noise Control Ordinance (NCO). A valid of calibration certificates including sound level meter and an acoustic were shown in *Appendix G*.

Monitoring Procedures

- 4.2.4 The noise measurement was performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq). Leq(30min) in six consecutive Leq(5 min) measurements were used as the monitoring parameter throughout the baseline monitoring period.
- 4.2.5 During the monitoring, the sound level meter was mounted on a tripod at a height of about 1.2 m and placed at the monitoring locations and oriented such that the microphone was pointed to the site with the microphone facing perpendicular to the line of sight. The windshield was fitted for the measurement. For construction noise monitoring, all monitoring stations were conducted 1 m from the exterior of the building façade.
- 4.2.6 Prior to noise measurement, the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. The calibration level from before and after the noise measurement agrees to within 1.0dB.
- 4.2.7 During the noise measurement, a portable wind speed meter was used to check wind speed (m/s). For impact noise monitoring, no wind speed was exceeding 5m/s or gusts exceeding 10m/s. Also, noise measurement in time was no fog and rain.

4.3 DATA MANAGEMENT AND DATA QA/QC CONTROL

- 4.3.1 The monitoring data were handled by the ET's in-house data recording and management system.
- 4.3.2 The monitoring data recorded in the equipment were downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data were input into a computerized database properly maintained by the ET. The laboratory results were input directly into the computerized database and checked by personnel other than those who input the data.
- 4.3.3 For monitoring parameters that require laboratory analysis, the local laboratory shall follow the QA/QC requirements as set out under the HOKLAS scheme for the relevant laboratory tests.



5 IMPACT MONITORING RESULTS

5.1 GENERAL

5.1.1 Air quality and construction noise monitoring scheduled in the Reporting Period is enclosed in *Appendix H* and the monitoring results are shown in the following sub-sections.

5.2 **RESULTS OF AIR QUALITY MONITORING**

5.2.1 The results for 24-hour and 1-hour TSP are summarized in *Tables 5-1 to 5-2*. The 24-hour TSP data are shown in *Appendix I* and graph plots including 1-hour TSP and 24-hour TSP are shown in *Appendix J*.

	AM1			AM2				
DATE	Start	1 st	2^{nd}	3 rd	Start	1 st	2 nd	3 rd
	Time	Meas.	Meas.	Meas.	Time	Meas.	Meas.	Meas.
1-Aug-16	10:30	48	46	44	9:30	43	41	39
6-Aug-16	9:03	50	47	41	9:09	52	51	48
12-Aug-16	9:12	39	43	47	13:26	67	61	56
18-Aug-16	9:45	37	43	45	13:33	54	59	49
24-Aug-16	9:11	47	52	55	13:24	64	67	72
30-Aug-16	9:36	44	51	55	13:19	69	62	54
Average	46				5	6		
(Range)	(37 - 55)				(39	- 72)		

Table 5-1Summary of 1-Hour TSP Monitoring Results, $\mu g/m^3$

Table 5-2Summary of 24-hour TSP Monitoring Results, µg/m³

Date	AM1	AM2a
4-Aug-16	36	19
10-Aug-16	*	28
12-Aug-16	49	NA
16-Aug-16	35	23
22-Aug-16	32	20
27-Aug-16	84	27
Average	47	23
(Range)	(32 - 84)	(19 – 28)

* No data collected on 10 August 2016 at AM1 due to power failure. Additional 24-hour TSP at AM1 was carried out on 12 August 2016.

- 5.2.2 As shown in *Tables 5-1* and *5-2*, the 24-hour and 1-hour TSP monitoring results were below the Action/ Limit Level. No Notification of Exceedances (NOE) of air quality criteria or corrective action was therefore required.
- 5.2.3 The meteorological data during the Reporting Month is summarized in *Appendix K*.
- 5.2.4 Construction dust assessment for short term impact was undertaken in the EIA study. In view of the current contract, monitoring locations AM1 and AM2a are not an ASR during the EIA study and therefore no prediction was made. For 1-hour TSP monitoring location AM2, it is very near the assessment point FLN-E13 in the EIA. According to the EIA prediction, the predicted result for Tier 2 in assessment year 2018 is 91.0µg/m³ for 1-hour TSP and the cumulative 1-hour concentrations would comply with the respective criteria and adverse short-term construction dust impact is not anticipated. It is concluded that the overall 1-hour TSP monitoring result in the Reporting Period is comparable to the EIA prediction.



5.3 **RESULTS OF CONSTRUCTION NOISE MONITORING**

5.3.1 In the Reporting Period, a total of 10 event noise measurements were carried out at the two designated locations. During construction noise monitoring, the sound level meter was set in 1m from the exterior of the building façade. Therefore, no façade correction (+3dB(A)) is added according to acoustical principles and EPD guidelines. The construction noise monitoring results at the designated locations are summarized in *Table 5-3*. The detailed noise monitoring data are presented in *Appendix I* and the relevant graphical plots are shown in *Appendix J*.

NM1			NM2		
Date	Time of Measurement	(L _{eq30min})	Time of Measurement	(L _{eq30min})	
1-Aug-16	9:30	52	10:30	52	
12-Aug-16	9:39	56	13:48	52	
18-Aug-16	10:18	55	13:36	49	
24-Aug-16	9:39	56	13:41	49	
30-Aug-16	9:41	56	13:21	50	
Limit Level	75 dB(A)				

Table 5-3Summary of Construction Noise Monitoring Results, dB(A)

5.3.2 As shown in *Table 5-3*, the noise level measured at the designated monitoring locations are well below 75dB(A). Furthermore, there was no noise complaints (Action Level exceedance) received by the RE, Contractors or DSD in the Reporting Period. Therefore, no Action or Limit Level exceedance was triggered and no corrective action was required.



6 WASTE MANAGEMENT

6.1 GENERAL WASTE MANAGEMENT

6.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

6.2 **RECORDS OF WASTE QUANTITIES**

- 6.2.1 All types of waste arising from the construction work are classified into the following:
 - Construction & Demolition (C&D) Material;
 - Chemical Waste;
 - General Refuse; and
 - Excavated Soil.
- 6.2.2 The quantities of waste for disposal in this Reporting Period are summarized in *Tables 6-1* and *6-2* and the Monthly Summary Waste Flow Table is shown in *Appendix L*. Whenever possible, materials were reused on-site as far as practicable.

 Table 6-1
 Summary of Quantities of Inert C&D Materials for the Project

		Disposal		
Type of Waste	Prior	Reporting	Cumulated	Location
	Months	Month	Cumulateu	Location
C&D Materials (Inert) (in '000m ³)	11.602	0.396	11.998	
Hard Rock and Large Broken Concrete	1.374	0.005	1.379	Tuen Mun
(Inert) (in '000m3)				38
Reused in this Project (Inert) (in '000 m ³)	0.672	0.100	0.772	
Reused in other Projects (Inert) (in '000 m ³)	2.228	0	2.228	
Disposal as Public Fill (Inert) (in '000 m ³)	7.418	0.291	7.709	Tuen Mun 38

Table 6-2 Summary of Quantities of C&D Wastes for the Project

		Disposal		
Type of Waste	Prior Months	Reporting Month	Cumulated	Disposal Location
Metals ('000kg)	113.51	4.72	118.23	Licensed collector
Paper / Cardboard Packing ('000kg)	0	0	0	
Plastics ('000kg)	0	0	0	
Chemical Wastes ('000kg)	0	0	0	
General Refuses ('000m ³)	0.119	0.012	0.131	NENT



7 SITE INSPECTION

7.1 **REQUIREMENTS**

7.1.1 According to the Updated EM&A Manual, the environmental site inspection shall be formulated by ET Leader. Weekly environmental site inspections should carry out to confirm the environmental performance.

7.2 FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH

- 7.2.1 In the Reporting Period, joint site inspection to evaluate the site environmental performance by the RE, ET and the Contractor has been carried out on 4, 9, 16, 23 and 30 August 2016. Furthermore, IEC attend site inspection was on 30 August 2016. No non-compliance was noted.
- 7.2.2 Observations for the site inspections and monthly audit within this Reporting Period are summarized in *Table 7-1*.

Date	Findings / Deficiencies	Follow-Up Status
4 August 2016	• No adverse environmental issue was obseved during site inspection.	• Nil.
9 August 2016	• Oil stain was observed on the ground. The contractor was advised to clean the oil stain and dispose as chemical waste.	• Oil stain was removed.
	• The contractor was reminded to spray water on unpaved haul road regularly.	• Not required for reminder.
16 August 2016	• Sludge were observed on the ground. The contractor was advised to clear the sludge.	• Sludge was removed from the ground.
	• The contractor was advised to spray mosquito oil on stagnant water.	• Mosquito oil was sprayed on the stagnant water
23 August 2016	• The Contractor was reminded to carry out water spraying regularly on site to reduce dust generation.	• Not required for reminder.
30 August 2016	• Crane idling without engine turned off was observed. The Contractor should turn off the idling vehicle to reduce air impact on site.	• To be follow in next reporting period.
	• The Contractor was reminded to remove the spilled chemical and treat as chemical waste at MFB to aviod land contamination.	

Table 7-1Site Observations

7.2.3 In the Reporting Period, the overall environmental performance was considered satisfactory.



8 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

8.1 Environmental Complaint, Summons and Prosecution

8.1.1 No environmental complaint, summons and prosecution was received in this reporting period. The statistical summary table of environmental complaint is presented in *Tables 8-1, 8-2* and *8-3*.

Table 8-1 Statistical Summary of Environmental Complaints

Donorting Doriod	Enviro	nmental Complaint St	tatistics
Reporting Period	Frequency	Cumulative	Complaint Nature
1 to 31 August 2016	0	0	NA

Table 8-2 Statistical Summary of Environmental Summons

Domonting Doniod	Enviro	onmental Summons S	tatistics
Reporting Period	Frequency	Cumulative	Complaint Nature
1 to 31 August 2016	0	0	NA

Table 8-3 Statistical Summary of Environmental Prosecution

Departing Devied	Enviro	nmental Prosecution S	Statistics
Reporting Period	Frequency	Cumulative	Complaint Nature
1 to 31 August 2016	0	0	NA



9 IMPLEMENTATION STATUS OF MITIGATION MEASURES

9.1 GENERAL REQUIREMENTS

- 9.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the Updated EM&A Manual covered the issues of dust, noise, water and waste and they are summarized presented in *Appendix M*.
- 9.1.2 The Contract under the Project shall be implementing the required environmental mitigation measures according to the Updated EM&A Manual as subject to the site condition. Environmental mitigation measures generally implemented by the Contract in this Reporting Period are summarized in *Table 9-1*.

Issues	Environmental Mitigation Measures
Water	• Wastewater to be treated by the filtration systems i.e. sedimentation tank
Quality	before to discharge.
Air Quality	Maintain wet surface on access road
	• All vehicles must be used wheel washing facility before off site
	Spray water during breaking works
	• A cleaning truck was regularly performed on the public road to prevent
	fugitive dust emission
Noise	• Restrain operation time of plants from 07:00 to 19:00 on any working day
	except for Public Holiday and Sunday.
	Keep good maintenance of plants
	• Shut down the plants when not in used.
Waste and	On-site sorting prior to disposal
Chemical	 Follow requirements and procedures of the "Trip-ticket System"
Management	Predict required quantity of concrete accurately
-	• Collect the unused fresh concrete at designated locations in the sites for
	subsequent disposal
General	The site was generally kept tidy and clean.

 Table 9-1
 Environmental Mitigation Measures

9.1.3 Based on monitoring results including air quality and construction noise, it is considered that the environmental mitigation measures implemented by the Contractor in this Reporting Period are effective.

9.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

- 9.2.1 Construction activities listed below will be undertaken in in the coming month for the Contract of the Project.
 - Erection of Formwork and Falsework (At Membrane Facilities Building)
 - Re-bar Fixing Works for Base Slab (At Membrane Facilities Building)
 - Concreting the Base Slab and Pile Cap (At Membrane Facilities Building)
 - Excavation, Installation of Sheet Pile and Pipe Laying for DN900 Trench (Near Final Sedimentation Tank No.5)
 - Restore BR2 and Suspend BR1 (At BR1 and BR2 Common Channel)
 - Suspension of twins DN1200 Effluent Pipe by Installation of Steel Plate (at Mix Liquor Channel)
 - General Cleaning and Dismantle Works (At Bioreactor No.1)
 - Excavation and Pipe Laying for DN150 Cable Duct (Near Final Sedimentation Tank No.6)
 - Construction of Field Equipment Pit#1 (V.O.6, Near Control Room No.2)



9.3 KEY ISSUES FOR THE COMING MONTH

- 9.3.1 Key issues to be considered in the coming month for the Contract include:
 - Implementation of dust suppression measures at all times;
 - Potential fugitive dust quality impact due from the dry/loose/exposure soil surface/dusty material;
 - Ensure dust suppression measures are implemented properly;
 - Implementation of construction noise preventative control measures;
 - Management of chemical wastes;
 - Follow-up of improvement on general waste management issues; and
 - Potential wastewater quality impact due to surface runoff



10 CONCLUSIONS AND RECOMMENTATIONS

10.1 CONCLUSIONS

- 10.1.1 This is the **11th** Monthly EM&A report, covering the construction period from **1 to 31 August 2016**.
- 10.1.2 No 24-hour or 1-hour TSP monitoring results that triggered the Action or Limit Levels were recorded. No NOEs or the associated corrective actions were therefore issued.
- 10.1.3 No noise complaint (which is an Action Level exceedance) was received and no construction noise measurement results that exceeded the Limit Level were recorded in this Reporting Period. No NOEs or the associated corrective actions were therefore issued.
- 10.1.4 No documented complaint, notification of summons or successful prosecution was received.
- 10.1.5 In the Reporting Period, joint site inspection to evaluate the site environmental performance by the RE, ET and the Contractor was carried out on 4, 9, 16, 23 and 30 August 2016. Furthermore, IEC attend site inspection was on 30 August 2016. No non-compliance was noted.
- 10.1.6 No site inspection was undertaken by any external party in this Reporting Period.

10.2 RECOMMENDATIONS

- 10.2.1 As wet season is approached, special attention should be paid to avoid ingress of surface runoff into nearby water bodies from the construction site. Water quality mitigation measures should be fully implemented.
- 10.2.2 Moreover, air quality mitigation measures including wheel wash facilities, watering of haul roads and covering of dusty materials with tarpaulin sheet, etc. should be properly maintained.
- 10.2.3 To control the site performance on waste management, Tsun Yip shall ensure that all solid and liquid waste management works are fully in compliance with the relevant license/permit requirements, such as the effluent discharge licence and the chemical waste producer registration. Tsun Yip is also reminded to implement the recommended environmental mitigation measures according to the Updating Environmental Monitoring and Audit Manual.




Appendix A

GENERAL LAYOUT OF ADVANCE WORKS AND MAIN WORKS OF SWHSTW FURTHER EXPANSION PHASE 1A

 $Z:\label{eq:label} Z:\label{eq:label} Z:\label{eq$




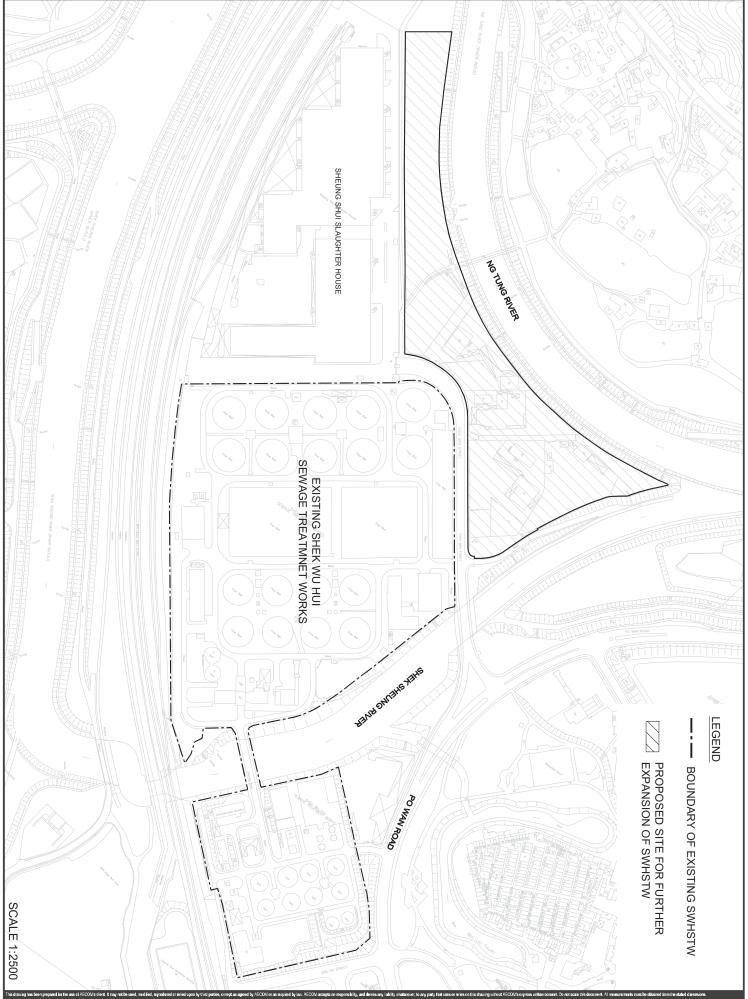

AGREEMENT NO. CE 40/2012 (DS) SHEK WU HUI SEWAGE TREATMENT WORKS - FURTHER EXPANSION PHASE 1A - INVESTIGATION Project No.: 60284037 Date: FEB. 2014

LOCATION OF THE EXISTING SWHSTW AND THE PROPOSED SITE FOR FURTHER EXPANSION

AECOM Drawing 60284037/EM&AM/400

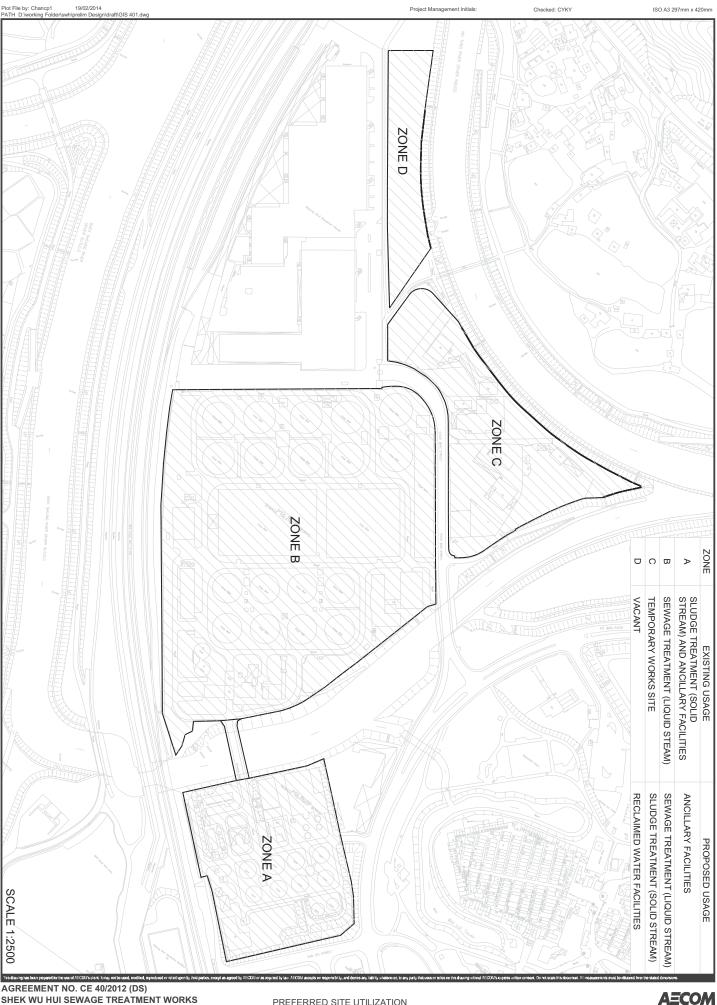

AGREEMENT NO. CE 40/2012 (DS) SHEK WU HUI SEWAGE TREATMENT WORKS - FURTHER EXPANSION PHASE 1A - INVESTIGATION Project No.: 60284037 Date: FEB. 2014

PREFERRED SITE UTILIZATION ACCORDING TO BRIEF



Appendix B

LAYOUT PLAN OF ADVANCE WORKS







Appendix C


ORGANIZATION STRUCTURE AND CONTACT DETAILS OF RELEVANT PARTIES

 $Z: \label{eq:loss} 2015 \ (Shek Wu Hui) \ (600 \ EM\&A Report \ Impact \ Monthly EM\&A Report \ 11 th EM\&A \ (August \ 2016) \ R0054v \ 2.doc \ 2$



Tsun Yip Waterworks Construction Company Limited 進業水務建築有限公司

Contract No. DC/2013/09 Advance Works for Shek Wu Hui Sewage Treatment Works - Further Expansion Phase 1A and Sewerage Works at Ping Che Road <u>SITE ENVIRONMENTAL TEAM ORGANIZATION CHART</u>

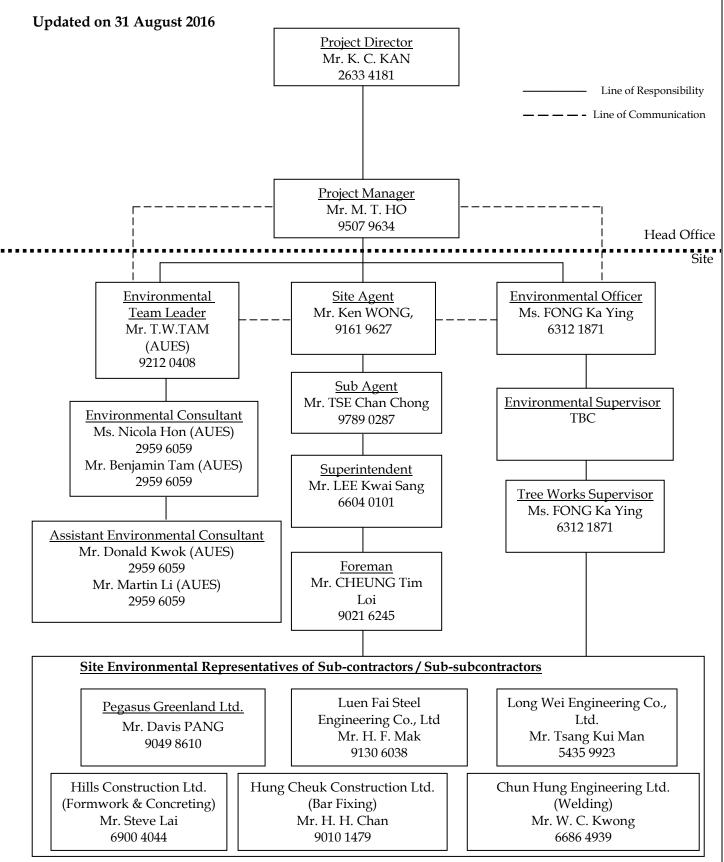



Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
DSD	Resident Site Engineer	Mr. Michael Leung	2594 7463	2827 8700
ANewR	Independent Environmental Checker	Mr. Adi Lee	2618 2836	3007 8648
Tsun Yip	Project Director	Mr. K. C. KAN	2633 4181	2633 4691
Tsun Yip	Project Manager	Mr. M. T. HO	9507 9634	2633 4691
Tsun Yip	Site Agent	Mr. Ken WONG	9161 9627	2633 4691
Tsun Yip	Environmental Officer	Ms. FONG Ka Ying	6312 1871	2633 4691
AUES	Environmental Team Leader	Mr. T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Mr. Ben Tam	2959 6059	2959 6079
AUES	Assistant Environmental Consultant	Mr. Martin Li	2959 6059	2959 6079

Contact Details of Relevant Parties

Legend:

DSD (Employer & Resident Site Engineer) – Drainage Service Department Tsun Yip (Main Contractor) – Tsun Yip Waterworks Construction Co Ltd

ANEWR (IEC) – ANEWR Consulting Limited

AUES (ET) – Action-United Environmental Services & Consulting




Appendix D

MASTER CONSTRUCTION PROGRAM

1 (D) Preliminary Items 89 days Tue 21/715 Sat 17/10/15 2 connact connectement 1 day Tue 21/715 Sat 17/10/15 3 6 ohney connectement 1 day Tue 21/715 Non 79/15 5 connact connectement Teu 21/715 Non 79/15 Non 79/15 6 Baselinament of Environmental Tem (ET) 1 days Tue 21/715 Non 79/15 6 Baselinament of Environmental Tem (ET) 1 days Tue 21/715 Non 79/15 7 Submission of Updated EM&A.Manual and Approval 21 days Tue 21/715 Non 79/15 7 Baselinament of Environmental Tem (ET) 9 days Tue 21/715 Non 79/15 8 Prostructural and Condition Nontering Prostructural Approval Prostructural Tem (ET) Non 79/15 7 Apprention Survey for Find Che Rout and Reporting Prostructural Tem (ET) Non 79/15 Non 79/15 10 Condition Survey for Find Che Rout and Reporting Prostructurat APR (PA) True 21/715 Non 79/15 11 (Find Pappead EC) Condition Survey Specialist and Approv	
Contract Commencent1 dayTue $21/715$ (a) Inderweitiding of Environmental Monitoring & Audit(a) Inderweitiding (b) daysTue $21/715$ (a) Inderweitiding of Environmental Tean (ET)(b) daysTue $21/715$ Subinission of Updated EM&A Manual and Approval(b) daysTue $21/715$ Subinission of Updated EM&A Manual and Approval(b) Structural and Condition Survey Specialist and Approval(b) daysTue $21/715$ (b) Structural and Condition Survey for Fing Che Road and Reporting(b) Structural and Condition Survey for Fing Che Road and Reporting(b) daysTue $21/715$ (c) Ontino Survey for Fing Che Road and Reporting(c) Chu Wan Street Site Offices (Portion B)(c) Chu Wan Street Site Offices (Portion B)(c) Chu Wan Street Site Offices (Portion B)StaysTue $21/715$ (c) Chu Wan Street Site Offices (Portion B)(c) Chu Wan Street Site Offices (Portion B)(c) Chu Wan Street Site Offices (Portion B)StaysTue $21/715$ (c) Chu Wan Street Site Offices (Portion B)(c) Chu Wan Street Site Offices (Portion B)StaysTue $21/715$ (d) Fing Che Road and General Pavenent Works(c) Chu Wan Street Site Office(c) daysTue $21/715$ (e) Chu Wan Street Site Office(c) Chu Wan Street Site Office(c) daysTue $21/715$ (f) Road Che Road Site Office(f) Road Che Road Site Office(f) Road Che Road Site OfficeTue $21/715$ (f) Road Che Road Site Office(f) Road Che Road Site Office(f) Road Che Road Site OfficeTue $21/715$ (f) Road Che Road Site Office(f) Road Che Road Site Office(f) Road Che Road Si	
(a) Implementation of Excitonmental Monitoring & Audit 0 days \mathbf{Tue} 21/715Establishment of Environmental Team (ET)Establishment of Environmental Team (ET) 1 days \mathbf{Tue} 21/715Submission of Updated EN&A Manual and Approval 1 days \mathbf{Tue} 21/715 1 days \mathbf{Tue} 21/715Submission of Updated EN&A Manual and Approval 1 days \mathbf{Tue} 21/715 1 days \mathbf{Tue} 21/715Resulting MonitoringRoot dition Survey for Ping Che Road and Reporting 8 days \mathbf{Tue} 21/715Condition Survey for Ping Che Road and Reporting 4 days \mathbf{Tue} 21/715Condition Survey for Ping Che Road and Reporting 4 days \mathbf{Tue} 21/715Sin Clearance / Cable Detection / Surveying Works 7 days \mathbf{Tue} 21/715Sin Clearance / Cable Detection / Surveying Works 7 days \mathbf{Tue} 21/715Application for Electricity / Water Supply/ Boardand Sevice 4 days \mathbf{Tue} 21/715Construction of Sinbeud and General Pavement Works 7 days \mathbf{Tue} 21/715Construction of Signboud and General Pavement Works 7 days \mathbf{Tue} 21/715Construction of Signboud and General Pavement Works 7 days \mathbf{Tue} 21/715Site Clearance / Cable Detection / Surveying Works 7 days \mathbf{Tue} 21/715Construction of Signboud and General Pavement Works 7 days \mathbf{Tue} 21/715Construction of Signboud and General Pavement Works 7 days \mathbf{Tue} 21/715Site Clearance / Cable Detection / Surveying Works 7 days <td< td=""><td></td></td<>	
Reaction of Updated ENKeA Manual and Approval 14 days Tue 21/71/1 Submission of Updated ENKeA Manual and Approval 14 days Tue 21/71/5 Reschins Moniforing 89 days Tue 21/71/5 Robust of Conditions Survey for Fing Candition Moniforing 89 days Tue 21/71/5 Proposal of Conditions Survey for Fing Candition Containent Works 7 days 7 days 7 fug Surves Removation Works for Engineer Office Removation Works for Engineer Office 7 days 7 fug Surves 7 days 7 fug Surves Removation Works for Engineer Office Removation Works for Engineer Office 7	
Baseline Monitoring 14 days Tue 23/N15 Proposal of Conditions Survey breinilist and Approval 14 days Tue 23/N15 Proposal of Conditions Survey breinilist and Approval 14 days Tue 23/N15 Proposal of Conditions Survey breinilist and Approval 14 days Tue 23/N15 Condition Survey for Fing Che Road and Reporting 45 days Tue 41/N15 Condition Survey for Fing Che Road and Reporting 45 days Tue 41/N15 Site Clearance / Cable Detection / Surveying Works 7 days Tue 23/N15 Application for Electricity / Water Supply/ Boardband Sevice 45 days Tue 23/N15 Application for Electricity / Water Supply/ Boardband Sevice 5 days Tue 23/N15 Application for Chettricity / Water Supply/ Boardband Sevice 5 days Tue 23/N15 Application for Chettricity / Water Supply/ Boardband Sevice 5 days Tue 23/N15 Application for Contination Office 82 days Tue 23/N15 Application for Contraction Office 10 days Tue 23/N15 Application for Electricity / Water Supply/ Boardband Sevice 15 days Tue 23/N15 Application for Electricity / Water Supply/ Boardband Sevice 15 days Tue 23/N15 Applica	
(b) Structural and Condition Monitoring 80 days Tue 21/715 Proposal of Conditions Survey Specialist and Approval 14 days Tue 21/715 Proposal of Conditions Survey Specialist and Approval 14 days Tue 41/715 Condition Survey for Fig. Cle Road and Reporting 45 days Tue 41/715 Condition Survey for Fig. Cle Road and Reporting 55 days Thu 34/715 Condition Survey for Fig. Cle Road and Reporting 55 days Thu 34/715 Site Clearance / Cable Detection / Surveying Works 7 days Tue 21/715 Application for Electricity/ Ware Supply/ Boardenad Sevice 57 days Tue 21/715 Application for Electricity/ Ware Supply/ Boardenad Sevice 60 days True 21/715 Construction of Signboard and General Parement Works 5 days True 21/715 Removation Works for Electricity/ Ware Supply/ Boardenad Sevice 5 days True 21/715 Site Clearance / Cable Detection Dice 5 days True 21/715 Site Clearance / Cable Detection Dice 5 days True 21/715 Site Clearance / Cable Detection Dice 2 days True 21/715 Site Clearance / Cable Detection Dice 2 days True 21/715 Site Clearance / Cable Detection Dice 2 days True 21/715 Site Clearance / Cable Detection Dice 2 days True 21/715	
Proposal of Conditions Survey Specialist and Approval 14 days Tue 417/15 Condition Survey for SWHSTW and Reporting 45 days Tue 417/15 Condition Survey for SWHSTW and Reporting 45 days Tue 417/15 Condition Survey for SWHSTW 82 days Tue 417/15 Condition Survey for SWHSTW 82 days Tue 317/15 Condition Survey for Fing Che Roud and Reporting 82 days Tue 317/15 Site Clearance / Cable Election / Surveying Works 7 days Tue 217/15 Application for Electricity / Ware Supply/ Boardband Sevice 7 days Tue 217/15 Application for Clanearo Office 60 days Tue 217/15 Reamovation Works for Electricity / Ware Supply/ Boardband Sevice 60 days Tue 287/15 Application for Struction of Signboard and General Pavement Works 16 days Tue 287/15 Reamovation Works for Electricity / Ware Supply/ Boardband Sevice 21 days Tue 287/15 State Clearance / Cable Detection Points 21 days Tue 287/15 State Clearance / Cable Detection Points 21 days Tue 287/15 State Clearance / Cable Detection Points 21 days Tue 287/15 <	
Condition Survey for SWHSTW and Reporting 45 days Tue 4/8/15 Condition Survey for Ping Chee Read and Reporting 45 days Tue 3/8/15 Condition Survey for Ping Chee Read and Reporting 45 days Tue 3/8/15 Condition Survey for Ping Chee Read and Reporting 45 days Tue 3/8/15 Sile Clearanee/ Cable Detection/ Surveying Works 7 days Tue 2/8/15 Application for Electricity / Water Supply/ Boardband Sevice 55 days Tue 2/8/15 Removation Works for Electricity / Water Supply/ Boardband Sevice 60 days Tue 2/8/15 Removation Works for Electricity / Water Supply/ Boardband Sevice 55 days The 2/8/15 Removation Works for Electricity / Water Supply/ Boardband Sevice 55 days The 2/8/15 Application for Electricity / Water Supply/ Boardband Sevice 55 days The 2/8/15 Application for Electricity / Water Supply/ Boardband Sevice 51 days The 2/8/15 Application for Electricity/ Water Supply/ Boardband Sevice 21 days The 2/8/15 Application for Electricity/ Water Supply/ Boardband Sevice 21 days The 2/8/15 Application for Electricity/ Water Supply/ Boardband Sevice 21 days The 2/8/15 Application for Electricity/ Water Supply/ Boardband Sevice 21 days The 2/8/15 Application for Electricity/ Water Supply/ Boardband Sevice	
Condition Survey for Ping Clue Road and Reporting Thu 3/9/15 (c) Chuw Mans Street Site Offices (Protion B) 24 and 5	
(c) Character Site Offices (Ortice) Contractor (Narwaying Works 82 days Tue 217715 Site Clearance (Cable Detection) Surveying Works 7 days Tue 217715 Application for Electricity Water Supply/ Boardmad Sevice 7 days Tue 217715 Application for Electricity Water Supply/ Boardmad Sevice 6 days Tue 217715 Construction of Contractor Office 45 days Tue 287715 Construction of Contractor Office 60 days Tue 287715 Construction of Signboard and General Pavement Works 16 days Tue 287715 Construction of Signboard and General Pavement Works 17 days The 287715 Construction of Signboard and General Pavement Works 17 days The 287715 Application for Electricity Water Supply/ Boardward Sevice 21 days Tue 287715 Application for Electricity Water Supply/ Boardward Sevice 21 days Tue 287715 Application for Electricity Water Supply/ Boardward Sevice 21 days Tue 287715 Application for Electricity Water Supply/ Boardward Sevice 21 days Tue 287715 Application for Electricity Water Supply/ Boardward Sevice 21 days Tue 287715 Application for Electricity Water Supply/ Boardward Sevice 21 days Tue 287715 Application for Electricity Water Supply/ Boardward Sevice 21 days Tue 287715	
Sile Clearance (Cable Detection) Surveying Works T days T days T use 21/7/15 Application for Electricity Water Supply / Bourdband Sevice 55 days Tue 28/7/15 Construction of Contractor Office 45 days Tue 28/7/15 Removation Works for Engineer Office 60 days Tue 28/7/15 Construction of Signboard and General Pavement Works 15 days The 28/7/15 Construction of Signboard and General Pavement Works 15 days The 28/7/15 Removation Works for Engineer Office 17.0 28 days The 28/7/15 Removation Works for Engineer Office 21 days The 28/7/15 Application for Electricity Water Supply Bourdband Sevice 21 days The 28/7/15 Application for Electricity Water Supply Bourdband Sevice 21 days The 28/7/15 Application for Electricity Water Supply Bourdband Sevice 21 days The 28/7/15 Application for Electricity Water Supply Bourdband Sevice 21 days The 28/7/15 Application for Electricity Water Supply Bourdband Sevice 21 days The 28/7/15 Application for Electricity Water Supply Bourdband Sevice 21 days The 28/7/15 Application for Electricity Water Supply Bourdband Sevice 21 days The 28/7/15 Application for Electricity Water Supply Bourdband Sevice 21 days The 28/7/15 </td <td></td>	
Application for Electricity Mater supply Boardeniad Sevice 7.6 days The 28//1.12 Construction of Contractor Office 6.6 days The 28//1.15 Removation Works for Engineer Office 6.0 days The 28//1.15 Removation of Signboard and General Pavement Works 15 days The 28//1.15 (1) Ping Cer Road Site Office (Portion D) 28 days The 21//1.15 Site Clearance / Cable Detection D) 28 days The 21//1.15 Site Clearance / Cable Detection D) 28 days The 21//1.15 Site Clearance / Cable Detection D) 28 days The 21//1.15 Site Clearance / Cable Detection D) 28 days The 21//1.15 Site Clearance / Cable Detection D) 28 days The 21//1.15 Site Clearance / Cable Detection D) 21 days The 28//1.15 Removation Works for Engineer Office (Containers) 21 days The 28//1.15 (1) Morks in Shek Wu Hui Sewage Treatment Works 750 days The 21//1.15 Constance / Abstin Direction D 700 days The 21//1.15	
Construction of Signburd and General Pavement Works e0 days The 287/13 Removation Works for Engineer Office e0 days The 287/13 Removation Works for Engineer Office 15 days Fri 119/15 Construction of Signburd and General Pavement Works 15 days Fri 119/15 Sine Clearance/ Cable Detection D) 28 days The 217/15 Sine Clearance/ Cable Detection D) 28 days The 217/15 Sine Clearance/ Cable Detection D) 28 days The 217/15 Sine Clearance/ Cable Detection Varea Supply Boardmand Sevice 21 days The 217/15 Application for Electricity/ Water Supply Boardmand Sevice 21 days The 287/15 Removation Works for Engineer Office (Containers) 21 days The 287/15 (1) Works in Shek Wu Hui Sewage Treatment Works 759 days The 2177/15	
Removation konst for Engineer Office Construction of Signiburu and Decement Works 0 days Tue 25//1/3 (d) Ping Che Read Site Office (Portion D) 28 days The 21/71/5 Site Clearance/ Cable Detection / Surveying Works 7 days Tue 21/71/5 Application for Electricity / Water Supply / Boardband Sevice 21 days Tue 21/71/5 Removation Works for Electricity / Water Supply / Boardband Sevice 21 days Tue 21/71/5 Removation Works for Electricity / Water Supply / Boardband Sevice 21 days Tue 21/71/5 Removation Works for Electricity / Water Supply / Boardband Sevice 21 days Tue 28/71/5 Removation Works for Electricity / Water Supply / Boardband Sevice 21 days Tue 28/71/5 Removation Works for Electricity / Water Supply / Boardband Sevice 21 days Tue 28/71/5 Removation Works in Electricity / Water Supply / Boardband Sevice 21 days Tue 28/71/5 Removation Works in Shek Wu Hui Sewage Treatment Works 759 days Tue 21/71/5	
Construction of Signboard and Centeral Parement Works Lo days Fm 117/13 (d) Ping Che Road Site Office (Portion D) Site office (Portion D) Site office (Portion D) (d) Ping Che Road Site Office (Portion D) Site office (Portion D) Site office (Portion D) Site Charanee/Cable Detection/Surveying Works 7 days Two 217/15 Application for Electricity/Water Supply/Boardband Sevice 21 days Two 237/15 Removation Works for Engineer Office (Containers) 21 days Two 237/15 (f) Works in Shek Wu Hui Sewage Treatment Works 759 days Two 217/15 Condon A Ano Anno Anno Anno Anno Anno	
(a) Fing Care Road Site Under (FOTGALD) 7 days 1 us 217/15 Site Clarance Cable Detection Surveying Works 7 days 1 us 217/15 Application for Electricity Water Supply Boardmad Sevice 21 days 1 us 287/15 Rennovation Works for Engineer Office (Containers) 21 days 1 us 287/15 (I) Works in Shek Wu Hui Sewage Treatment Works 759 days 1 us 21/715 (I) Works in Shek Wu Hui Sewage Treatment Works 750 days 1 us 21/715	
Application for Electricity Water Supply Boardband Sevice 1 4 ms 1 ms 287/15 Application for Electricity Water Supply Boardband Sevice 21 days 1 ms 287/15 Removation Works for Engineer Office (Containers) 21 days 1 ms 287/15 (11) Works in Shek Wu Hui Sewage Treatment Works 759 days 1 ms 217/15 (2000 containers) 759 days 1 ms 217/15	
21 days Tue 28/7/15 759 days Tue 21/7/15 400 Anno Tue 21/7/15	
759 days Tue 21/7/15 400 Anno Tue 21/7/15	
759 days Tue 21/7/15	
The supervision of the supervisi	
blishment 245 days Tue 21/7/15	
sment with ST1 14 days Tue 21/7/15	
nd Documents 21 days Tue 1/3/16	Ĩ
7 days Tue 15/3/16	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1
Koom to new MFB) 245 days	
Dural Laying (EXERTING CONTOL KONTI O F31 /) YO 40/S (EVENTING CONTOL KONTI O F31 / VALUE V F32 / VA	
out to the company of	
:MFB) 45 days Sat 8/10/16 Mt	
639 days Tue 21/7/15 W	
35 days Tue 21/7/15	
ment with ST1 28 days Tue 21/7/15	
nd Documents 28 days Tue 21/7/15	
Application for SWAC and PWAC Application for SWAC Application for SWAC Applicati	
cr/o/or and cran tro	
and FST2/ Suspension of BR2 5 days Tue 25/8/15	
Closing / Disconnect Power and Signal) 5 days Sun 30/8/15	
int to SWHSWTW 7 days Fri 4/9/15 7	
139 days Tue 18/8/15	
14 days	
f Pipe / DN800 FST Influent Pipe 7 days Fri 4/9/15	
25 days Fri 11/9/15	
Instal Sheeping and Struth in the structure and Larks an	
CLUTTOLITI SUD CF	
of GL Locations 5 days Mon 4/1/16	
es 20 days Sat 9/1/16 T1	
ag Levels 7 days Fri 29/1/16	
115 days Fri 29/1/16 S	
n Works 7 days Fri 29/1/16 7	
Construction of Fuel Control of Construction 2000 (2000) (200) (2000) (2	
os) 35 days Sun 6/3/16	

Task Name	Vame	Duration	Start	Finish 2015 2016 2016 6 7 8 9 10 11 12 3 4 5 7	201 8 9 10 11 12 1 2 3 4 5 6
	Grouting / Curing for Piles (2nd Batch)	30 days	Sun 10/4/16		
	Pile Testing and Proof drilling	25 days	Thu 28/4/16	Sun 22/5/16	
	Setting-up of Prik-Load Test System (1st & 2nd pue) Pile-Load Test for Main Piles (1st and 2nd nile)	/ days 3 days	1nu 28/4/16 Pri 6/5/16	Mon 9/2/16	
	Removal and Resetting of Pile-Load Test System	5 days	Tue 10/5/16		
	Pile-Load Test for Main Pile (3rd and 4 pile)	3 days	Sun 15/5/16	Tue 17/5/16	·····
	Removal of Pile-Load Test System	5 days	Wed 18/5/16	· · · · · · · · · · · · · · · · · · ·	· · · · · · · · · · · · · · · · · · ·
	Proof Drilling	5 days	Sun 15/5/16	Thu 19/5/16	
	(v) Construction of Subtructure Portion A - Grid C.E / Grid F-G / Grid G+14 - G+28	110 days	Mon 23/5/16		
	Excavation to Formation Level (+0.3/+2.4mPD)	15 days	Mon 23/5/16	Mon 6/6/16	·····
	Laying Blinding Layer	2 days	Tue 7/6/16	Wed 8/6/16	
Ц	Preparation for Pilehead	5 days	Thu 9/6/16	Mon 13/6/16	
	Steelfixing for Membrance Facilitates (up to +1.9mPD) and Membrance Tank (up to +3.9mPD)	10 days	Tue 14/6/16	Thu 23/6/16	
	Installation of formwork / waterstop / other accessory	7 days	Fri 24/6/16		
	Concrenus Onino of concrete / formwork removal / makino acoch works	3 dave	Mon 4/7/16		
	Counds of consistent for memory for the second states of the forther secon	15 davs	Thu 7/7/16		
	Installation of formwork / waterstop / other accessory	10 days	Fri 22/7/16	Sun 31/7/16	
	Concreting	3 days	Mon 1/8/16		
	Curing of concrete / formwork removal / making good works	5 days	Thu 4/8/16		
	Steelfixing for Membrance Facilitates & Tanks (up to +6.77.5mPD)	15 days	Tue 9/8/16	Tue 23/8/16	
	Installation of formwork / waterstop / other accessory	10 days	Wed 24/8/16	Fri 2/9/16	
	Concreting	2 days	Sat 3/9/16	Sun 4/9/16	×-1
	Curing of concrete / formwork removal / making good works	s days	Mon 5/9/16	01/k/k/ EFI	
	Excavation to Formation Level (+0.3/+2.4mPD)	20 days	Tue 7/6/16	Sun 26/6/16	
	Laying Blinding Layer	2 days	Mon 27/6/16	Tue 28/6/16	
	Preparation for Pilehead	5 days	Wed 29/6/16	Sun 3/7/16	
	Steelfixing for Membrance Facilitates (up to +1.9mPD) and Membrance Tank (up to +3.9mPD)	10 days	Mon 4/7/16	Wed 13/7/16	
	Installation of formwork / waterstop / other accessory	7 days	Thu 14/7/16	Wed 20/7/16	
	Concreting	3 days	Thu 21///16	Sat 23/1/16	
	Curing of concrete / formwork removal / making good works Cooldining for Montheman Evidence & Truto (m. 16. 14, 75 anDD)	5 days	01///12 unc		
	otecutating for memorance racintates & faints (up to ±0.40 + 1.2007 D) Installation of fermionel (unterston / other accessory	10 dave	Thu 11/8/16		
	помпанол от голи work / wavestop / оцист ассезот у Concreting	3 days	Sun 21/8/16	Jue 23/8/16	
	Curing of concrete / formwork removal / making good works	5 days	Wed 24/8/16	Sun 28/8/16	
	Steelfixing for Membrance Facilitates & Tanks (up to +6.777.5mPD)	15 days	Mon 29/8/16	Mon 12/9/16	
	Installation of formwork / waterstop / other accessory	10 days	Tue 13/9/16	Thu 22/9/16	
	Concreting	2 days	Fri 23/9/16	Sat 24/9/16	
	Curing of concrete / formwork removal / making good works	5 days	Sun 25/9/16	Thu 29/9/16	
	Backfilling and Extracting Sheetphile	25 days	Fri 30/9/16	Mon 24/10/16	
	(v) Construction of Superstructure E-mot Working Diaform and Education (m. to. 11, 65m DD)	15 days	FTI 30/9/16	Tue 4/4/17 Emiliario	
	LICCE WORDING FLAUTORING AND LARGEN (UP to 711.0010112) Steelffixing for Membrance Facilitates Bldgs	15 davs	Sat 15/10/16		
	Installation of formwork / other accessory	15 days	Sun 30/10/16	Sun 13/11/16	- 1
	Concreting	2 days	Mon 14/11/16	Tue 15/11/16	
	Curing of concrete / formwork removal / making good works	7 days	Wed 16/11/16	Tue 22/1/1/6	•••
	Steelfixing for Membrance Facilitates Bldgs (up tp +12.95mPD)	10 days	Wed 23/11/16	Fri 2/12/16	×í
	Installation of formwork / other accessory	7 days	Sat 3/12/16	Fri 9/12/16	•••••
	Concreting	2 days	Sat 10/12/16	Sun 1/12/16	
	Curing of concrete / formwork removal / making good works	5 days	Mon 12/12/16	Fii 16/12/16	
	Steentxing for Memorance Facilitates Biggs (up tp +14.45mr/D) Installation of formword: / other accessory	7 dave	Sat 1 // 12/10 Time 77/17/16		5 ->1
	Concreting	2 days	Tue 3/1/17	Wed 4/1/17	→×
	Curing of concrete / formwork removal / making good works	5 days	Thu 5/1/17	Mon 9/1/17	*
	Erect Working Platform and Falsework (up to +19.2mPD)	15 days	Thu 5/1/17	Thu 19/1/17	s C
	Steelfixing for Membrance Facilitates Bldgs (up tp +19.2mPD)	15 days	Fri 20/1/17	Fii 3/2/17	f
		P			

	ID Task Name		Duration	Start	t Finish 2015 2015 2016 2016 2016 2016 2016 2016 2016 2017 2017 2017 2017 2017 2017 2017 2017	2017
			1 day	Sat 4/2/17		0 0
			2 days	Sun 5/2/17	Mon 6/2/17	•••••
		ng good works	7 days	Tue 7/2/17		
		ap up + + + + + + + + + + + + + + + + + +	7 days	Wed 1/3/17		
Total control contro control control control control control control co			2 days	Wed 8/3/17	× ×	
		ng good works	7 days	Fri 10/3/17		•••••
		up tp +26.00mPD)	7 days	Fri 17/3/17		
			S days	Fit 24/3/17 Wed 29/3/17		
		ng good works	5 days	Fri 31/3/17		
wurd freihen interleichen, die	(iiv)		92 days	Tue 25/10/16		•••••
Numerication Control			60 days	Tue 25/10/16		•••••
Image: media metal		nk	15 days	Tue 10/1/17		
Theorem Theorem <t< td=""><td></td><td></td><td>15 days</td><td>Wed 5/4/17</td><td></td><td></td></t<>			15 days	Wed 5/4/17		
			15 days	Wed 5/4/17		
Image: Construction of REI in Connection on aged time sido) 5 4.9 mod 20125 Empty REI in Connection on aged time sido) 5 4.9 mod 20125 Empty REI in Connection on aged time sido) 5 4.9 mod 20125 Supremise of REI in Connection on aged time sido) 5 4.9 mod 20125 Supremise of REI in Connection on aged time sido) 5 4.9 mod 20125 Supremise of REI in Connection on aged time sido) 5 4.9 mod 20125 Supremise of REI in Connection on aged time sido) 5 4.9 mod 20125 Supremise of REI in Connection 12 4.9 mod 20125 Supremise of REI and DRC2 3 4.9 mod 20125 Connection an Elever Connection 3 4.9 mod 20125 Gill Realing DNE REI profer Connection (on aged time sido) 3 4.9 mod 20125 Connection an Elever Connection on aged time sido) 3 4.9 mod 20125 Connection an Elever Connection (on aged time sido) 3 4.9 mod 20125 Connection an Elever Connection (on aged time sido) 3 4.9 mod 20125 Connection an Elever Connection (on aged time sido) 3 4.9 mod 20125 Connection an Elever Connection (on aged time sido) 3 4.9 mod 20125 Connection an Elever Connection (on aged time sido) 3 4.9 mod 20125 Connection an Elever Connection (on aged time sido) 3 4.9 mod 20125 Connection an Elever Connection (on aged time sido) 3 4.9 mod 20125 On Mode Stand Elever Connection (on			15 days	Wed 5/4/17		•••••
Table			118 dave	1 ue 21///15 Sun 30/8/15		
Suspension of BR Lot Sprention (on aged time sko) 5 4.9 well R1/1/5 Suspension of BR Lot Currenction (on aged time sko) 5 4.9 Wed R1/1/5 Suspension of BR Lot Currenction (on aged time sko) 5 4.9 Wed R1/1/5 Water Joint 7 2 4.9 Wed R1/1/5 Pipe Langue Works for BR and DR2 3 4.9 Wed R1/1/5 Fipe Langue Works for BR and DR2 3 4.9 Wed R1/1/5 Separative Works for BR and DR2 3 4.9 Wed R1/1/5 Connection at Ligator Chand 3 4.9 That S2/1/5 Connection at Ligator Chand 3 4.9 That S2/1/5 Connection of assection Chand 3 4.9 That S2/1/5 Connection at Ligator Chand 3 4.9 That S2/1/5 Connection at Ligator Chand			10 days	Sun 30/8/15	Tue skyrts	•••••
State State Mun 21/215 State State Tex 21/715 Pipe Lation Oberting Material Oberting State Ved 18/11/15 Pipe Lation Oberting Material Oberting State Ved 18/11/15 Pipe Lation Oberting Material Oberting State Ved 18/11/15 Pipe Lation Oberting Note the RNL and RN2 State Ved 18/11/15 Pipe Lation Oberting Note the RNL and RN2 State Ved 18/11/15 Connection at RN2 Connection at RN2 State Ved 18/11/15 Connection at RN2 Connection at RN2 State Ved 18/11/15 Connection at RN2 Onwork by ST1 State Ved 18/11/15 Connection at RN2 Onwork by ST1 State Ved 18/11/15 Connection at RN2 Onwork by ST1 State Ved 18/11/15 Connection at RN2 Onwork by ST1 State Ved 18/11/15 Connection at Lation Connection on agree time stot) Text gas Non 21/12/15 Pipe Laying for SN Pipe C(PIPO-ID) Text gas Non 21/12/15 Pipe Laying for SN Pipe C(PIPO-ID) Text gas Non 21/12/15 Pipe Laying for SN Pipe C(PIPO-ID) Text gas Non 21/12/15 Pipe Laying for SN Pipe C(PIPO-ID) Text gas		me slot)	5 days	Wed 18/11/15	Sun 22/11/15	•••••
(ii) Ple Laying for RR2 Play (CHC00.33) The 2LY/T/S Pre Laying for RR2 Play (CHC00.33) 3 days Wed RV1/T/S Pre Laying for RR2 Play (CHC00.33) 3 days Wed RV1/T/S Pre Texting (iii) Connection Works 8 days Wed RV1/T/S Septome Works for RR1 and RR2 3 days Wed RV1/T/S 3 days Wed RV1/T/S Septome Works for RR1 and RR2 3 days Wed RV1/T/S 3 days Wed RV1/T/S Septome Works for RR1 and RR2 3 days Wed RV1/T/S 3 days Wed RV1/T/S Connection and Layor Chunnel 5 days Wed RV1/T/S 3 days Wed RV1/T/S Connection and Layor Chunnel 5 days Wed RV1/T/S 3 days Wed RV1/T/S Pre Laying Ker SK Pipe (CH70-IG7) 3 days Wed RV1/T/S 3 days Wed RV1/T/S Pipe Laying Ker SK Pipe (CH70-IG7) 3 days Wed RV1/T/S 3 days Wed RV1/T/S Pipe Laying Ker RU Pipe CH70-IG7) 7 days S days Wed RV1/T/S Pipe Laying Ker RU Pipe CH70-IG7) 7 days S days Wed RV1/T/S Pipe Laying Ker RU Pipe CH70-IG7) 7 days S days S days Pipe Laying Ker RU Pipe CH70-IG7) 7 days S days S days Pipe Laying Ker RU Pipe CH70-IG7) 7 days <td></td> <td>time slot)</td> <td>5 days</td> <td>Mon 21/12/15</td> <td>Hi 25/12/15</td> <td></td>		time slot)	5 days	Mon 21/12/15	Hi 25/12/15	
Mathematical Ordering Proteinal Ordering Fig. Fissing (1) Connection MSB Pipe (CHC00-33) Each Similary MSB Pipe (CHC00-33) Each Similary MSB Pipe (CHC00-33) Fig. Tessing (1) Connection at Pipe Separate Work for RR1 and RR2 3 days Weil (R11/15) Separate Work for RR1 and RR2 3 days Weil (R11/15) Connection at Pipe Connection at Pipe (CHC00-51) 3 days Weil (R11/15) Separate Work for RR1 and RR2 3 days Weil (R11/15) Connection at Pipe Connection at Pipe (1) Pipe Laying for SAS Pipe (2) Pipe Laying for SAS Pipe Pipe (2) Pipe Pipe (2) Pipe Pipe (2) P			153 days	Tue 21/7/15	Sun 2012/IS	•••••
Tele			120 days	Tue 21/7/15		•••••
(ii) Currention Works 8 days wei 18/11/5 Separate Works for BR1 and BR2 5 days Wei 18/11/5 Connection an Liquor Channel 5 days Wei 18/11/5 Connection an Liquor Channel 5 days Wei 18/11/5 Separate Works by SFII 0 (N Realings DS169 SAS Pipe 3 days Wei 18/11/5 Separate in of associated system for Channel 5 days Mon 21/12/15 (i) Realings DS169 SAS Pipe 3 days Mon 21/12/15 (ii) Pipe Laying for SAS Pipe CHOLOCHTO) 3 days Mon 21/12/15 (iii) Pipe Laying for SAS Pipe CHOLOCHTO) 3 days Mon 21/12/15 (iii) Pipe Laying for SAS Pipe CHOLOCHTO) 3 days Mon 21/12/15 (iii) Pipe Laying for SAS Pipe CHOLOCHTO) 3 days Mon 21/12/15 (iii) Pipe Laying for SAS Pipe CHOLOCHTO) 3 days Mon 21/12/15 (iii) Pipe Laying for SAS Pipe CHOLOCHTO) 3 days Mon 21/12/15 (iii) Pipe Laying for SAS Pipe CHOLOCHTO) 3 days Mon 21/12/15 (iii) Pipe Laying for SAS Pipe 3 days Mon 21/12/15 (iii) Pipe CHOLOCHTO) 1 days S days S days (iii) Pipe CHOLOCHTO) 1 days S days S days (iii) Pipe CHOLOCHTO) 1 days S days S days (iii) Pipe CHOLOCHTO			30 days 3 days	Fri 18/12/15		
Separate Works for BR1 and BR2 5 days Wed 18/1/1.5 Connection at 18/02 5 days Mon 21/1.215 Stapstation of asserting of system for Connection (on agree time slot) 3 days Thu 18/2/16 Stapstation of asserting of system for Connection (on agree time slot) 3 days Mon 21/12/15 Stapstation of asserting and new SAS Pipe 3 days Mon 21/12/15 Stapstation of asserting and new SAS Pipe 3 days Mon 21/12/15 Connection (1) Pipe Laying for SAS Pipe (CHPOL IG) 3 days Mon 21/12/15 Stapstation of SAS Pipe (CHPOL IG) 3 days Mon 21/12/15 3 days Mon 21/12/15 Pipe Laying for BR1 Pipe (CHPOL IG) Pipe Laying for BR1 Pipe (CHPOL IG) 3 days Mon 21/12/15 Stapstation of SAS Pipe (CHPOL IG) Pipe Laying for BR1 Pipe (CHPOL IG) 3 days Sin 21/16 Pipe Laying for BR1 Pipe (CHPOL IG) Pipe Laying for BR1 Pipe (CHPOL IG) 3 days Sin 21/16 State of Vorkie Net/ID Pipe Laying for BR1 Pipe (CHPOL IG) 3 days Sin 21/16 Pipe Laying Work Piper Pipe (CHPOL IG) Pipe Laying for BR1 Pipe (CHPOL IG) 2 days <td< td=""><td></td><td></td><td>38 days</td><td>Wed 18/11/15</td><td>Fri 25/12/15</td><td></td></td<>			38 days	Wed 18/11/15	Fri 25/12/15	
Connection at R82 3 days Mon 21/12/15 Connection at Ligon Channel 5 days Mon 21/12/15 (d) Nealing Exsting DN156.85 Ppe 5 days Mon 21/12/15 (f) Nealing Exsting DN156.85 Ppe 3 days Thu 182/16 (g) Nealing Exsting DN156.85 Ppe 3 days Thu 182/16 (g) Pipe Laying For SAS Pipe (CH0-CH70) 3 days Mon 21/12/15 Pipe Laying for SAS Pipe (CH0-CH70) 25 days Mon 21/12/15 Pipe Laying for SAS Pipe 3 days Mon 21/12/15 Pipe Laying for SAS Pipe 3 days Mon 21/12/15 Pipe Laying for SAS Pipe 3 days Mon 21/12/15 Connection 3 days Mon 21/12/15 Pipe Laying for SAS Pipe 3 days Mon 21/12/15 Pipe Laying for SAS Pipe 10 Nicole			5 days	Wed 18/11/15	Sum 22/11/15	
(1) Realign Existing DNL958.SS Pipe 2 days Mmo 2/1/215 (2) Works by ST1 (3) Works by ST1 2 days Mmo 2/1/216 (3) Works by ST1 (3) Works by ST1 2 days Mmo 2/1/216 (4) Pre-Laying for SAS Pipe (1) Pre-Laying for SAS Pipe 2 days Mmo 2/1/216 (1) Pre-Laying for SAS Pipe (1) Pre-Laying for SAS Pipe 2 days Mmo 1/2/1216 (1) Pre-Laying for SAS Pipe (1) Pre-Laying for SAS Pipe 3 days Mmo 1/2/1216 (2) Pre-Laying for SAS Pipe (1) Pre-Laying for SAS Pipe 3 days Mmo 1/2/1216 (2) Pre-Laying for SAS Pipe (1) Pre-Laying for SAS Pipe 3 days Pmo 1/2/16 (2) Pre-Laying for SAS Pipe (1) Pre-Laying for SAS Pipe 3 days Pmo 1/2/16 (3) Researce Nal and Carterion on agree time stolo 3 days Pmo 1/2/16 (4) Researce Nal and Carterion SAS Pipe (1) Researce 3 days Pmo 1/2/16 (5) DNU-HaloD IS BRI Efficient DPipe 3 days Pmo 1/2/16 2 days S days Pmo 1/2/16 (5) ONU-HaloD IS BRI Efficient DPipe (1) Researce 3 days Pmo 1/2/16 2 days S days S days S days (1) Researce Nal and C (1) Researce Nal at 2 2 days S days S days S days S days			3 days	Mon 21/12/15	Wed 23/12/15	•••••
u) Works by STI 0. Works by STI 3 days Thu 182/16 Suspension of associated system for Connection 3 days Thu 182/16 Pipe Laying Works 3 days Thu 182/16 Suspension of associated system for Connection 3 days Thu 182/16 Pipe Laying for SAS Pipe CH00-CH70) 3 days Wm 21/12/15 Pipe Laying for SAS Pipe CH00-CH70 3 days Wm 21/12/15 Connection 3 days Wm 21/12/15 Pipe Laying for BR1 Pipe CH10-16.) 3 days Sm 21/2/16 Pipe Laying for BR1 Pipe CH10-16.0 3 days Sm 21/2/16 Pipe Laying for BR1 Pipe CH10-16.0 3 days Sm 21/2/16 Pipe Laying for BR1 Pipe CH10-16.0 3 days Sm 21/2/16 Pipe Laying for BR1 Pipe CH10-16.0 10 days Sm 21/2/16 Pipe Laying for BR1 Pipe CH10-16.0 10 days Sm 21/2/16 Pipe Laying for BR1 Pipe CH10-16.0 10 days Sm 21/2/16 Pipe Laying for BR1 Pipe CH10-16.0 10 days Sm 21/2/16 Pipe Laying for BR1 Pipe CH10-16.0 10 days Sm 21/2/16 Pipe Laying for BR1 Pipe CH10-16.0 10 days			5 days	Mon 21/12/15		
Suspension of saccited system for Connection (on agree time slot) 3 days Thu 18/21/6 (i) Phys Laying Works 2 days Mon 21/21/5 Pipe Laying for SAS Pipe (CH70-16/2) 3 days Mon 21/21/6 Pipe Laying for SAS Pipe (CH70-16/2) 3 days Mon 21/21/6 Pipe Laying for SAS Pipe (CH70-16/2) 3 days Mon 21/21/6 Pipe Laying for SAS Pipe (CH70-16/2) 3 days Mon 5/2/16 Connection 3 days Son 21/21/6 (i) Phys Laying for SAS Pipe (CH70-16/5) 3 days Son 21/21/6 (i) Mon SAS Pipe 0 mon SAS Pipe 3 days Son 21/21/6 (i) Mon SAS Pipe 0 mon SAS Pipe 3 days Son 21/21/6 (ii) Restare RR2 and Inew SAS Pipe (CH70-16) 3 days Son 21/21/6 (ii) Restare RR2 and Inew SAS Pipe 1 mon SAS 3 days Son 21/21/6 (ii) Restare RR2 and Iner SA 1 mon SAS 3 days Son 21/21/6 (ii) Restare RR2 and Iner SA 1 mon SAS 3 days Son 21/21/6 (ii) Restare RR2 and R			3 davs	Thu 18/2/16	Sat 20/2/16	
(i) Pipe Laying Works (2 days) Mon 2/12/15 Pipe Laying for SAS Pipe (CH/0: CH70) 2 days Mon 2/12/15 Pipe Laying for SAS Pipe (CH/0: CH70) 3 days Mon 2/12/16 Pipe Laying for SAS Pipe (CH/0: CH70) 3 days Mon 2/12/16 Testing and two SAS Pipe 3 days Mon 2/12/16 Connection 3 days Sin 1/2/16 (c) INM and DI SR IE filterent Pipe 3 days Sin 1/2/16 Pipe Laying for SR1 Pipe (CH10-16) 3 days Sin 2/12/16 (c) INM and DI SR IE filterent Pipe 3 days Sin 2/12/16 Pipe Laying for SR1 Pipe (CH10-16) 3 days Sin 2/12/16 (f) Bloweater No.1 and 2 10 3 days Sin 2/12/16 (f) Bloweater No.1 and 2 10 3 days Sin 2/12/16 (f) Bloweater No.1 and 2 10 10 2 days Sin 2/12/16 (f) Bloweater No.1 and 2 10 10 2 days Sin 2/12/16 (f) Bloweater No.1 and 2 10 10 Sin 2/2/15 2 days Sin 2/2/15 (f) Bloweater No.1 and 2 10 10 2 days Sin 2/2/16 (f) Bloweater No.1 and 2 10 10 2 days Sin 2/2/16 (f) Bloweater No.1 and 2 10 10 2 days		on (on agree time slot)	3 days	Thu 18/2/16	Sar 20/27/6	•••••
Pipe Laying for SAS Pipe (CH0)-CH70) 25 days Mon 21/21/5 Pipe Laying for SAS Pipe (CH0)-L(2) 3 days Min 51/16 Testing and new SAS Pipe 3 days Min 51/16 Testing and new SAS Pipe 3 days Min 51/16 Connection 3 days Min 51/16 Connection 3 days Sun 21/216 Pipe Laying for BR Pipe (CH400-16) 3 days Sun 21/216 Pipe Laying for BR Pipe (CH400-16) 3 days Sun 21/216 Pipe Laying for BR Pipe (CH400-16) 100 days Sun 21/216 Pipe Laying for BR Pipe (CH400-16) 100 days Sun 21/216 Pipe Laying for BR Pipe (CH400-16) 100 days Sun 21/216 (i) Nonsels W STI 100 days Sun 21/216 (ii) Nonsels W STI 100 days Sun 21/216 (iii) Nonsels W STI 100 days Sun 21/216 Sun days by STI 110 days Sun 21/216 (iii) Nonsels W STI 12 days Sun 21/216 (iii) Nonsels W STI 12 days Sun 21/216 (iii) Nonsels W STI 110 days Sun 21/216 (iiii) Nonsels W STI 110 days Sun 21/21	(II)		62 days	Mon 21/12/15	Sat 20/2/16	
Pipe Laying for SAS Pipe (CH70-162) 31 days Fit IS/1/16 Testing and new SAS Pipe 3 days Non IS/2/16 Connection 3 days San 21/2/16 Explore Laying for BR IP pro (CH700-16) 3 days San 21/2/16 Pipe Laying for BR IP pro (CH700-16) 3 days San 21/2/16 Pipe Laying for BR IP pro (CH700-16) 3 days San 21/2/16 Pipe Laying for BR IP pro (CH700-16) 3 days San 21/2/16 Pipe Laying for BR IP pro (CH700-16) 3 days San 21/2/16 Pipe Laying for BR IP pro (CH700-16) 3 days San 21/2/16 Pipe Laying for BR IP pro (CH700-16) 3 days San 21/2/16 Pipe Laying for BR IP pro (CH700-16) 10 days by STI 10 days San 21/2/16 Pipe Laying for BR IP pro (CH700-16) 10 days San 21/2/16 San 21/2/16 Pipe Laying for BR IP pro (CH700-16) 10 days San 21/2/16 San 21/2/16 Pipe Laying for BR IP pro (CH700-16) 11 days 12 days San 24/1/16 Pipe Laying for BR IP pro (CH700-16) 12 days San 24/1/16 Pipe Laying for BR IP pro (CH700-16) 12 days San 24/1/16 Pipe Laying for BR IP pro (CH700-16) 12 days San 24/1/16 Pipe Laying and Removal Existing DN12/20 DB Effituen Pipe 12 days			25 days	Mon 21/12/15	Thu 14/1/16	
I certing and new XAS Pipe 3 days Thu 18/2/10 Connection 3 days Sun 21/2/16 Pipe Laying for BR1 Pfment Pipe 3 days Sun 21/2/16 Pipe Laying for BR1 Pfment Pipe 3 days Sun 21/2/16 Pipe Laying for BR1 Pfment Pipe 3 days Sun 21/2/16 Pipe Laying for BR1 Pfment Pipe 3 days Sun 21/2/16 Pipe Laying for BR1 Pfment Pipe 3 days Sun 21/2/16 Pipe Laying for BR1 Pipe 3 days Sun 21/2/16 Pipe Laying for BR1 Pipe 3 days Sun 21/2/16 Pipe Laying for BR1 Pipe 3 days Sun 21/2/16 Pipe Laying for BR1 Pipe 3 days Sun 21/2/16 Pipe Laying equipment to SWHSWTW 15 days Sun 21/1/16 Distantie and Reume staining equipment to SWHSWTW 15 days Sun 71/1/16 Distantie and Reume staining equipment to SWHSWTW 15 days Sun 71/1/16 Pipe and Reumonal Existing DN12/00 BR Effluen Pipe 5 days Sun 71/1/16 Pipe and Reumonal Existing DN12/00 BR Effluen Pipe 5 days Sun 71/1/16 Pipe and Reumonal Existing DN12/00 BR Effluen Pipe 5 days Sun 71/1/16 Pipe and Reumonal Existing DN12/00 BR Effluen Pipe 5 days Sun 71/1/16 Pipe and Reumonal Existing DN12/00 BR Effluen Pipe 7 days			31 days	Fri 15/1/16	Sun 14/216	
(c) DN1400 DI BRI Effnent Ppe 30 days Sun 21/216 Pipe Laying for BR1 Ppe (CHF00-16) 30 days Sun 21/216 Pipe Laying for BR1 Ppe 30 days Sun 21/216 Pipe Laying for BR1 Ppe 30 days Sun 21/216 Pipe Laying for BR1 Ppe 30 days Sun 21/216 Pipe Laying for BR1 Ppe 30 days Sun 21/216 Pipe Laying for BR1 Ppe 31 days Sun 21/215 Pipe Laying for BR1 Ppe 7 days Sun 20/215 Pipe Laying equipment to SWFSWTW 15 days Sun 20/216 Dismande and Reum existing equipment to SWFSWTW 7 days Sun 10/116 Dismande and Reum existing equipment to SWFSWTW 17 days Sun 17/116 Ping and Renoval Existing Works Dismande Works 7 days Sun 17/116 Ping and Renoval Existing Works Dismande Works 7 days Sun 17/116 Ping and Renoval Existing Works Dismande Works 7 days Sun 17/116 Ping and Renoval Existing Works Dismande Works 7 days Sun 17/116 Ping and Renoval Existing Walks Repue 7 days Sun 21/116 Ping and Renoval Existing Walks Repue 7 days Sun 21/116 Ping and Renoval Existing Walks Repue 7 days Sun 21/116 Promotion of Working Walks Repue 7 days Sun 21/116			3 days	01/7/C1 UOM	weat 11/21/b	
Pipe Luying for BR1 Pipe (CHF00-16) 30 days Sur 21/21/6 (D) Biorenciero NA1 and 2 190 days Sur 20/21/5 (D) Noreks by STI 17 days Sur 20/21/5 (D) Noreks by STI 15 days Sur 20/21/5 (D) Noreks by STI 17 days Sur 20/21/5 (D) Noreks by STI 17 days Sur 20/12/6 (D) Standard and Reum existing equipment to SWHSWTW 7 days Sur 20/12/6 (D) Remayer BR1 7 days Sur 20/11/6 (D) Starter Br1 7 days Sur 20/11/6 (D) Starter Br1 7 days Sur 20/11/6 <tr< td=""><td></td><td></td><td>30 davs</td><td>Sun 21/2/16</td><td></td><td></td></tr<>			30 davs	Sun 21/2/16		
(f) Bioreactor No.1 and 2 149 days Sat 26/12/15 (i) Works by ST1 7 days Sat 26/12/15 (i) Works by ST1 7 days Sat 26/12/15 1 behation Works for BRU(Pipe Closing / Discoment Power and Signal) 7 days Sat 26/12/15 1 behation Works for BRU(Pipe Closing / Discoment Power and Signal) 7 days Sat 26/12/15 1 behation Works for BRU(Pipe Closing / Discoment Power and Signal) 7 days San 17/1/16 1 Bennovation Works for BRU 7 days San 17/1/16 1 Removation Works for BRU 7 days San 17/1/16 1 Bennovation Works for BRU 7 days San 17/1/16 1 Bennovation Works for BRU 7 days San 17/1/16 1 Bennovation Works for BRU 7 days San 24/1/16 1 Bennovation Works for BRU 7 days San 24/1/16 1 Bennovation of Working Platform and Flakework 7 days San 24/1/16 1 Bennolise of upper Burlise 7 days San 24/1/16 1 Bennolise of upper and Existing Walk & Pepare Surface 7 days San 24/1/16 1 Benlise of Concrete walkway sectended from walls 7 days San 24/1/16 1 Benlise of concret walkway sectended from walls <td< td=""><td></td><td></td><td>30 days</td><td>Sun 21/2/16</td><td>Mon 21/3/16</td><td>•••••</td></td<>			30 days	Sun 21/2/16	Mon 21/3/16	•••••
(i) Works by ST1 27 days Sar 26/12/15 Restere BR2 and Empty BR1 15 days Sar 26/12/15 Restere BR2 and Empty BR1 15 days Sar 26/12/15 Restere BR2 and Empty BR1 7 days San 7/11/16 Distantion Works inside BR1 7 days San 7/11/16 Restere BR2 and Empty BR1 127 days San 7/11/16 General Cleaning Works inside BR1 127 days San 7/11/16 General Cleaning Works inside BR1 127 days San 7/11/16 Restere BV2 and Renovalizing DV1200 BR Efficient Pipe 5 days San 7/11/16 Restere Vallway 127 days San 7/11/16 San 7/11/16 Restere Vallway 127 days San 7/11/16 San 7/11/16 Restere Vallway 128 days San 7/11/16 San 7/11/16 Restere Vallway 128 days San 7/11/16 San 7/11/16 Restere Vallway 128 days San 7/11/16 San 7/11/16 Restere Vallway 110 days San 7/11/16 San 7/11/16 Restere Vallway 110 days San 7/11/16 San 7/11/16 Restere Vallway 110 days San 7/11/16 San 7/			149 days	Sat 26/12/15	Sun 22/5/16	
Restore BK2 and Empty BK1 15 days Sut 2012/15 Isolation Works for BK1 (Pipe Closing / Disconnect Power and Signal) 7 days Sun 10/1/16 Dismantie and Removation Works inside BK1 12 days Sun 17/1/16 (ii) Removation Works inside BK1 127 days Sun 17/1/16 Gareat Cleaning Works / Disconnect Power and Signal) 5 days Sun 17/1/16 Flags and Removal Existing DN1200 BR Effluent Pipe 2 days Sun 17/1/16 Flags and Removal Existing DN1200 BR Effluent Pipe 8 days Sun 17/1/16 Exterior of Working Plationm and Falsework 15 days Sun 17/1/16 Exercision of working Plationm and Falsework 15 days Sun 17/1/16 Exercision of working Plationm and Falsework 15 days Sun 17/1/16 Exercision of working Plationm and Falsework 15 days Sun 17/1/16 Exercision of working Plationm and Falsework 15 days Sun 17/1/16 Exercision of working Plationm and Falsework 15 days Sun 17/1/16 Exercision of working Plationm and Falsework 15 days Sun 17/1/16 Exercision of working Plationm and Falsework 15 days Sun 17/1/16 Exercision of working Plationm and Falsework 15 days Sun 17/1/16 Exercision of working Plation 16 days Sun 17/1/16 Exercision of wo	(I)		27 days	Sat 26/12/15		
Image: Discontext Forward Signal) Adjs Sun 101/16 Distantie and Return existing equipment to SWHSWTW Distantie and Return existing equipment to SWHSWTW (ii) Removation Works risking ENIZO RE Efficient Pipe Table State S			15 days	Sat 26/12/15	Sat 9/1/6	•••••
(ii) Removation Works inside BR1 127 days Sun 1711/16 (iii) Removation Works Inside BR1 7 days Sun 1711/16 (iii) Removation Works Distantie Works 7 days Sun 1711/16 (iii) Removation Works Distantie Works 7 days Sun 1711/16 (iii) Removation Works 8 days Sun 1711/16 (iii) Removation Works 8 days Sun 1711/16 Extended Concrete Walkway 8 days Sun 1711/16 Extended Concrete Walkway 15 days Sun 1711/16 Encerbook Voking Platkom and Falsework 15 days Sun 1711/16 Encert Puk for concrete Walkway extended from walls 2 days Sun 1711/16 Conneuting Consetting 7 days Sun 1371/16 Cuing of concrete Valkway errowal making good works 7 days Sun 1371/16 Cuing of concrete Plas 7 days Sun 1371/16 Consetting Construction of Concrete Plas 7 days Sun 1371/16 FRP Baffle Wall / Platforms / Sun removal / making good works 7 days Sun 1371/16 FRP Baffle Wall / Platforms / Sun removal 16 days Sun 1371/16 FRP Baffle Wall / Platforms / Sun removal 16 days Sun 1371/16 FRP Baffle Wall / Platforms / Sun removal 16 days Sun 1371/16		nnect Power and Signal) WHSWTW	7 days 5 days	Sun 10/1/16 Sun 17/1/16		•••••
General Cleaning Works/ Dismantle Works 7 days Sun 17/1/16 Plug and Removal Existing DN1200 BR Effluent Pipe 5 days Sun 17/1/16 Extended Concrete Walkway 5 days Sun 17/1/16 Extended Concrete Walkway 15 days Sun 24/1/16 Exection of Working Platform and Falsework 15 days Sun 24/1/16 Erection of Working Platform and Falsework 15 days Sun 24/1/16 Erection of Working Platform and Falsework 2 days Sun 24/1/16 Concreting 2 days Fri 4/3/16 Concreting 2 days Sun 13/1/16 Curing of concrete Valkway extended from walls 2 days Sun 13/16 Curing of concrete Valkway extended from walls 2 days Sun 13/16 Curing of concrete Plast 7 days Sun 13/16 Construction of Concrete Plast 7 days Sun 23/16 Priching Works for PR1 Task 10 days Sun 23/16 Priching Works for PR1 Task Sun 23/16 Priching Works for PR1 Task Sun 23/176 Priching Works for PR1 Task Sun 23/176	(ii)		127 days	Sun 17/1/16	Sun 22/5/16	
Plug and Removal Existing DN1.200 BR Eritheart Pipe S days Sun 171/16 Extended Concrete Walkway Extended Concrete Walkway S days Sun 171/16 Extended Concrete Walkway Extended Concrete Walkway S days Sun 241/16 Demoltion of upper part of Extended Form walk S days Sun 241/16 Demoltion of upper part of Extended from walks S days Sun 241/16 Concreting 2 days Prin 173/16 Concreting 2 days Fri 143/16 Curing of concrete valkway extended from walks 2 days Fri 173/16 Curing of concrete Valkway errowal making good works 7 days Snn 135/16 Insull See Prass 7 days Snn 137/16 Construction of Concrete Piss 7 days Snn 137/16 Priching Works for RR1 16 days Snn 137/16 Priching Works for RR1 15 days Snn 237/16 Priching Works for RR1 15 days Snn 237/16 Priching Works for RR1 15 days Snn 241/16 FRP Baffle Wall / Platforms / Staircase 15 days Sun 241/16			7 da ys	Sun 17/1/16	Sat 23/1/16	
Extended Concrete Walkway Stays Sun 241/16 Extended Concrete Nalkway Extended Concrete Nalkway Stays Fri 4/3/16 Event Pix K for concreting Concreting 7 days T days Fri 1/3/16 T days Stan 13/16 Install See Physis Install See Physis 7 days Stan 13/16 Stan 13/16 Install See Physis Construction of Concrete Pix / Ans of DNS00 MLR Pipes 7 days Sun 13/16 Pitching Works for RR1 15 days Sun 23/16 Sun 23/16 Pitching Works for RR1 15 days Sun 23/16 Pitching Works for RR1 15 days Sun 24/16 FRP Baffle Wall / Platforms / Staircase 13 days Sun 24/16		ent Pipe	5 days	Sun 17/1/16	The 21/1/16	•••••
Image: Demotion of upper gratement and environment of the period of the period form wills Demotion of upper gratement and environment of the period form wills Demotion of upper gratement and environment of the period form wills Demotion of upper gratement and environment of the period form wills Demotion of upper gratement of the period form wills Demotion of upper gratement of the period form wills Demotion of upper gratement of the period form wills Demotion of upper gratement of the period form wills Demotion of upper gratement of the period form wills Demotion of upper gratement of the period form wills Demotion of the period form will be period form will be period for the per	Exte		88 days	Sun 24/1/16	Wei 20416	•••••
Erect Fwk for concrete walkway extended from walls 7 days Fri 4/3/16 7 Concreting 2 days Fri 1/3/16 Concreting 2 days San 1/3/16 Currenting 7 days San 2/3/16 Install Steel Posts 7 days San 2/3/16 Pitching Works for BR1 15 days San 2/3/16 Pitching Works for BR1 15 days San 2/3/16 Task Milestore 120 days San 2/1/16	-	ork s & Prepare Surface	25 davs	Mon 8/2/16	017/1 mmc	
Concreting 2 days Fit 11/3/16 Cuing of concrete / formwork removal / making good works 2 days Fit 11/3/16 Install of concrete / formwork removal / making good works 7 days Sun 3/3/16 Install of concrete Pits / 4 Nos of DN800 MLR Pipes 7 days Sun 2/3/16 Pitching Works for BR1 10 days Sun 2/13/16 FRP Baffle Wall / Platforms/Suitcase 120 days Sun 2/13/16		1 from walls	7 days	Fri 4/3/16	Thu 10/3/16	
Curing of concrete / formwork removal / making good works 7 days Sun 13/3/16 Install Steel Pass 7 days Sun 13/3/16 Construction of Concrete Pits / A los of DN800 MLR Pipes 10 days Sun 20/3/16 Pitching Works for BR1 15 days Wed 64/16 FRP Baffle Wall / Platforms / Suircase 12 days Wed 64/16 Task Milestorne ♦ Summary			2 days	Fri 11/3/16	Sat 12/3/16	•••••
Construction of Concerte Pils / 4 Nos of DN800 MLR Pipes 10 days Sun 272/3/6 Pitching Works for BR1 15 days Wed 64/16 FRP Baffle Wall / Platforms/Staircase 120 days Sun 271/16		making good works	7 days	Sun 13/3/16 Sun 20/3/16		
Pitching Works for BR1 15 days Wed 64/16 FRP Baffle Wall / Platforms / Staircase 120 days Sun 24/1/16 Task Milestore ♦ Summary		DN800 MLR Pipes	10 days	Sun 27/3/16		
FRP Baffle Wall / Platforms / Staircase 120 days Sun 24/1/16			15 days	Wed 6/4/16	Wed 20/4/16	
Milestone			120 days	Sun 24/1/16		

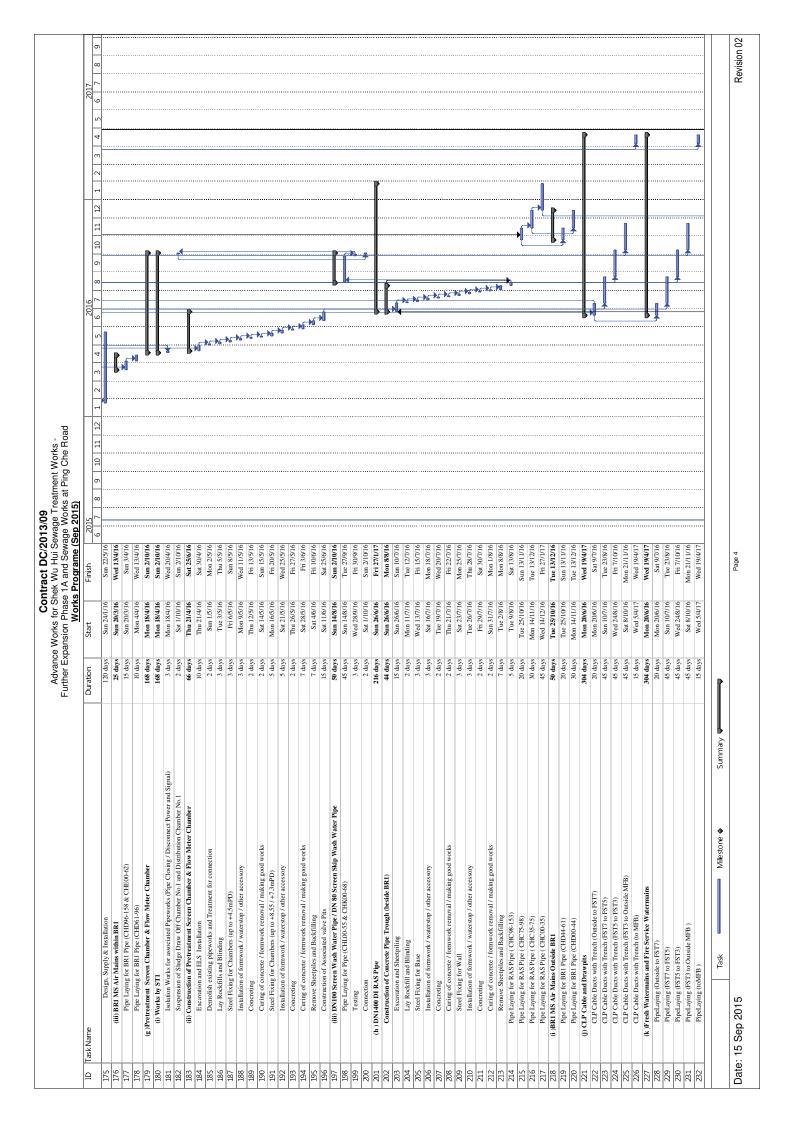

ID Task Name	Duration	Start	Finish	Finish 2015 2016 2017 <
233 (1)DN900 DI Permeate Pipe	157 days	Wed 24/8/16	Fri 27/1/17	
Pipe Laying (CHA85-CHA138)	45 days	Wed 24/8/16	Fri 7/10/16	
235 Pripe Laying (CHA35-CHA85) 236 Prine Laving (CHA30-CHA85)	45 days	Sat 8/10/16 Wed 14/12/16	Mon 21/11/16 Fri 27/1/17	
(an owned) Surface addr				
Section 3		Tue 21/7/15	Thu 17/8/17	
(a) Establishment Discussion for Working Conner and Sta Amanamant with CTI	35 days	Tue 21/7/15	Mon 24/8/15	
Discussion for working sequence and suc Arrangement with 511 Submission of Method Statement and Documents	28 davs	Tue 21/7/15	Mon 17/8/15	
Application for SWAC and PMAC	7 days	Tue 18/8/15	Mon 24/8/15	
(b) Demolition of Existing Reclaim Water Treatment Facilitates	58 days	Tue 25/8/15	Wed 21/10/15	
(i) Works by ST1	14 days	Tue 25/8/15	Mon 7/9/15	
Isolation Works for Reclamed Water Treamanet Facilates (Pipe Closing / Disconnect Power and Signal)	7 days	Tue 25/8/15	Mon 31/8/15	
Dismantle and Return existing equipment to SWHSWTW	7 days	Tue 1/9/15	Mon 7/9/15	
(ii) Demolition of Rectaim Water Treatment Facilitates General Dismontle and Site Romation Works	15 days	Tue 8/9/15 Tue 8/9/15	Tue 22/9/15 Tue 22/9/15	
(iii) Demolition of Methanol Storage Tanks	29 days	Wed 23/9/15	Wed 21/10/15	
General Dismante Works	7 days	Wed 23/9/15	Tue 29/9/15	
Erection of Working Platform	7 days	Wed 30/9/15	Tue 6/10/15	
Removal of Existing Concrete Structure	15 days	Wed 7/10/15	Wed 21/10/15	
(c) Building Works for Membrane Facilities and Tanks	120 days	Thu 20/4/17	Thu 17/8/17	
Kooting with sufface channel Leadington of Soundation and FDD finance	20 C2	Thu 20/4/17	/ 1/C/HI unc	
Instalation of Sundries and FKP nems Durning Station Internal finishing	45 days	Thu 20/4/17	Sat 3/0/17 Sat 3/6/17	
r unpug station internat misung Pumping Station External Wall finishing	75 davs	Sun 4/6/17	Thu 17/8/17	
(d) Remaining Cable and DrawPits	150 days	Sat 28/1/17	Mon 26/6/17	
Duct Laying (East amd South of BR11)	45 days	Sat 28/1/17	Mon 13/3/17	
Duct Laying (T Junction btw Membrane Tanks / BR1)	90 days	Wed 29/3/17	Mon 26/6/17	
(e) Chemical Storage Room	50 days	Thu 20/4/17	Thu 8/6/17	
Excavation / Preparation of Footing	5 days	Thu 20/4/17	Mon 24/4/17	
Laying blinding Swalfsting for E-oritor	2 days	Tue 25/4/1/	Ved 20/4/17	
Installation of fortwork / other accessory	2 davs	Sun 30/4/17	Mon 1/5/17	
Concreting	2 days	Tue 2/5/17	Wed 3/5/17	
Curing of concrete / formwork removal / making good works	2 days	Thu 4/5/17	Fri 5/5/17	
Steelfixing for Top Stab and Wall	5 days	Sat 6/5/17	Wed 10/5/17	**
Installation of formwork / other accessory	5 days	Thu 11/5/17	Mon 15/5/17	
Concreting	2 days	Tue 16/5/17	Wed 17/5/17	
Curing of concrete / formwork removal / making good works	2 days	Thu 18/5/17	Fri 19/5/17	
Building Service Works for Chemical Storage Room	20 days	Sat 20/5/17	Thu 8/6/17	
(f)DNIS0 DI SAS Pipe/NaOCI Dosing Pipe and Trench	90 days	Wed 29/3/17	Mon 26/6/17	
SAS Pipe (CHH00-49) / Dosing Pipe (CH00-68)	90 days	Wed 29/3/17	Mon 26/6/17	
(g) Dramage Works and Koauworks Storm Dusing and Roadworks (ECTS to ECT3)	45 days	Wed 24/0/16	11/0/1 101/1	
Storm Drains and Roadworks (FST3 to outside MFB)	45 davs	Sat 8/10/16	Mon 21/11/16	
Storm Drains and Roadworks (East and South of BR1)	60 days	Sat 28/1/17	Tue 28/3/17	
Storm Drains and Roadworks (T Junction btw Membrane Tanks / BR1)	90 days	Wed 29/3/17	Mon 26/6/17	
Storm Drains and Roadworks (Around Membrane Facilities and Tanks)	60 days	Fri 9/6/17	Mon 7/8/17	
Works in Fing Che Road		Tue 21/7/15	Wed 18/1/17	
Section 4 - Sewerage Works in Ping Che Road	548 days	Tue 21/7/15	Wed 18/1/17 Set 16/1/16	
(a) 11 c partation 11 of as Material Submission and Ordering	100 davs	Tue 21/7/15	Wed 28/10/15	· · · · · · · · · · · · · · · · · · ·
Application for XP	90 days	Tue 21/7/15	Sun 18/10/15	
Inspection Pits	90 days	Mon 19/10/15	Sat 16/1/16	
(b) Work Front A (CH00-CH765)	418 days	Tue 3/11/15	Sat 24/12/16	•
Pipe Laying for Rising Mains (CH165-CH185) / Under Dwarf Wall	10 days	Tue 3/11/15	Thu 12/11/15	
	econ cr	CTATLCT III	CT011/2 III	


		Sat 21/3/16 Sat 21/3/16 Sat 21/3/16 San 12/6/16 San 12/6/16 San 17/71/16 San 27/11/16 San 27/11/16 Sat 27/11/15 Sat 27/11/15 Sat 27/11/15 Sat 27/11/15 Sat 27/11/15 Fri 26/21/6 Fri 26/21/6 Fri 26/21/6 Fri 26/21/6 Mon 4/1/16 Fri 26/21/6 Fri 26/21/6 Mat 27/71/16 Fri 26/21/6 Fri 26/21/6 Fri 26/21/6 Fri 26/21/6 Fri 23/91/6 Fri 23/91/	Fri 25/16 Sun 225/16 Sun 225/16 Sun 225/16 Mon 13/6/16 Mon 13/6/16 Mon 13/6/16 Sun 13/6/16 Mon 25/116 Sun 13/6/16 Mon 25/116 Sun 13/6/16 Mon 25/116 Sun 13/115 Tue 3/11/15 Sun 8/11/15 Sun 8/11/15 Sun 8/11/15 Sun 9/16/16 Sun 9/6/16 Sun 25/716 Sun 9/6/16 Tue 8/71/16 Tue 8/11/16 Tue 8/71/16 Sun 9/6/16 Tue 8/71/16 Sun 9/6/16 Tue 8/71/16 Tue 8/71/16 Tue 8/71/16 Sun 9/6/16 Tue 8/71/16 Sun 9/6/16 Tue 8/71/16	38. days 7 days 35. days 35. days 40. days 15. days 15. days 15. days 15. days 20. days 15. days 15. days 15. days 16. days 17. days 18. days 19. days 20. days 21. days 22. days 23. days 23. days 24. days 25. days 26. days 27. days 28. days 29. days 20. days 20. days 21. days 22. days 23. days 24. days 26. days 27. days 28. days 29. days 29. days 20. days 21. days 22. days 23. days 24. days 26. days	 Pipe Laying for Rising Mains CH560 (TH50) //Juder Dwart Wall Inerim Pressure Test Pipe Laying for Rising Mains (CH560 CH570) //Luder Dwart Wall Pipe Laying for Rising Mains (CH560 CH570) //Luder Dwart Wall Pipe Laying for Rising Mains (CH560 CH570) //Luder Dwart Wall Pipe Laying for Rising Mains (CH500 CH570) //Luder Dwart Wall Pipe Laying for Rising Mains (CH500 CH570) //Luder Dwart Wall Pipe Laying for Rising Mains (CH500 CH570) //Luder Dwart Wall Pipe Laying for Rising Mains (CH500 CH570) //Luder Dwart Wall Pipe Laying for Rising Mains (CH500 CH500) //Luder Dwart Wall Pipe Laying for Rising Mains (CH500 CH500) //Luder Dwart Wall Pipe Laying for Rising Mains (CH500 CH500) //Luder Dwart Wall Pipe Laying for Rising Mains (CH500 CH500) //Luder Dwart Wall Pipe Laying for Rising Mains (CH100 CH1005) //Luder Dwart Wall Pipe Laying for Rising Mains (CH100 CH1005) //Luder Dwart Wall Pipe Laying for Rising Mains (CH100 CH1005) //Luder Dwart Wall Pipe Laying for Rising Mains (CH100 CH1005) //Luder Dwart Wall Pipe Laying for Rising Mains (CH100 CH1005) //Luder Dwart Wall Pipe Laying for Rising Mains (CH100 CH1055) //Luder Dwart Wall Pipe Laying for Rising Mains (CH105 CH1200) / Road Crossing Pipe Laying for Rising Mains (CH105 CH120) / Kaad Crossing Pipe Laying for Rising Mains (CH105 CH120) / Maer Dwart Wall Pipe Laying for Rising Mains (CH105 CH120) / Maer Dwart Wall Pipe Laying for Rising Mains (CH105 CH120) / Maer Dwart Wall Pipe Laying for Rising Mains (CH105 CH120) / Maer Dwart Wall Pipe Laying for Rising Mains (CH136 CH120) / Maer Dwart Wall Pipe Laying for Rising Mains (CH136 CH120) / Maer Dwart Wall Pipe Laying for Rising Mains (CH136 CH120) / Maer Dwart Wall Pipe Laying for Rising Mains (CH136 CH136) / Under Dwart Wall Pipe Laying for Rising Mains (CH136
	·····	Wed 18/1/17	Thu 5/1/17	14 days	/abbing
		Wed 4/1/17	Sat 26/11/16	40 days	s (CH765-CH845) / Under Dwarf Wall
		Fri 25/11/16	Fri 11/11/16	15 days	CH845-CH855) / Road Crossing
		Thu 10/11/16	61/6/6 II-I Sof 24/0/16	Stab CI	CH950-CH970)/ Koad Crossing
		Thu 8/9/16	Tue 30/8/16	10 days	CH1520-CH1540) / Under Draft Wall
× *		Mon 29/8/16	Sat 20/8/16	10 days	TH1495-CH1520) / Footpath
		Fri 19/8/16	Tue 26/7/16	25 days	CH1440-CH1495) / Under Dwarf Wall
		Mon 25/7/16	Thu 21/7/16	5 days	(CH1430-CH1440) / Fooipath
		Wed 20/7/16	Mon 11/7/16	10 da vs	(CH1362-CH1410)/ Koad Clossing (CH1410-CH1430) / Under Dwarf Wall
		Sat 25/6/16	Sun 19/6/16	7 days	
		Sat 18/6/16	Wed 25/5/16	25 days	s (CH1335-CH1385) /Under Dwarf Wall
-1		Tue 24/5/16	Thu 5/5/16	20 days	as (CH1290-CH1335) / River Crossing
		Tue 19/4/16 Wed 4/5/16	Fii 18/3/16 Wed 20/4/16	33 days 15 days	is (CH1205-CH1270) /Under Dwarf Wall ss (CH1270-CH1290) / Road Crossing
		Thu 17/3/16	Sat 27/2/16	20 days	s (CH1180-CH1205) / Road Crossing
	1	Fri 26/2/16	Sat 30/1/16	28 days	is (CH1095-CH1180) / Footpath
	ſ	Fri 29/1/16	Wed 20/1/16	sy ab CI 10 davs	is (CH1075-CH1075) / Road Crossing is (CH1075-CH1095) /Under Dwarf Wall
	ſ	Mon 4/1/16	Sun 13/12/15 True 5/1/16	23 days	ns (CH1010-CH1055) /Under Dwarf Wall
	4 1	Sat 12/12/15	Sat 28/11/15	15 days	ns (CH1000-CH1010) / Road Crossing
	-16-	Fri 27/11/15	Mon 23/11/15	5 days	ns (CH990-CH1000) /Under Dwarf Wall
	-Á	Sun 22/11/15	Sun 8/11/15	15 days	is (CH980-CH990)/Road Crossing
		Sat 7/11/15	Tue 3/11/15	5 davs	1540) s (CH970-CH980) /Under Dwarf Wall
		Sat 24/12/16	Sun 18/12/16	7 days	
		Sat 17/12/16	Mon 28/11/16	20 days	is (CH00-CH60) / Footpath
		Mon 10/10/16	Mon 26/9/16	15 days	s (CH155-CH165)/Road Crossing
		Sun 25/9/16	Sun 11/9/16	15 days	s (CH750-CH765) / Road Crossing
÷1		Sat 10/9/16	Tue 2/8/16	40 days	as (CH670-CH750) /Under Dwarf Wall
		Mon 1/8/16	Mon 18/7/16	15 days	ns (CH660-CH670) / Road Crossing
		Sun 17/7/16	Mon 13/6/16	35 days	ins (CH590-CH590) / Footpain ins (CH590-CH660) /Under Dwarf Wall
		Sat 28/5/16	Sun 22/5/16	7 days	(CH560 CH500) / Excende
		Sat 21/5/16	Fri 25/3/16	58 days	ns (CH445-CH560) /Under Dwarf Wall
		Thu 24/3/16	Thu 10/3/16	15 days	Pipe Laying for Rising Mains (CH425-CH445) / Road Crossing
	1	Wed 9/3/16	Thu 4/2/16	35 days	Pipe Laying for Rising Mains (CH360-CH425) / Under Dwarf Wall
	.	Wed 3/2/16	Fri 15/1/16	20 days	Pipe Laying for Rising Mains (CH300-CH360) / Footpath
	+1	Thu 14/1/16	Tue 5/1/16	10 days	Pipe Laying for Rising Mains (CH295-CH300) / Road Crossing
	-f	Mon 4/1/16	Fri 18/12/15	18 days	Pipe Laying for Rising Mains (CH245-CH295) / Footpath
	· · · ·	Thu 17/12/15 :	Sat 28/11/15	20 days	Pipe Laying for Rising Mains (CH205-CH245) / Under Dwarf Wall
		r v	2 17 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1		



Appendix E

PROPOSED MONITORING LOCATIONS


 $Z:\label{eq:label} Z:\label{eq:label} Z:\label{eq:label} Solution (Shek Wu Hui)\label{eq:label} Solution (Shek Wu Hui)\label{eq:label$

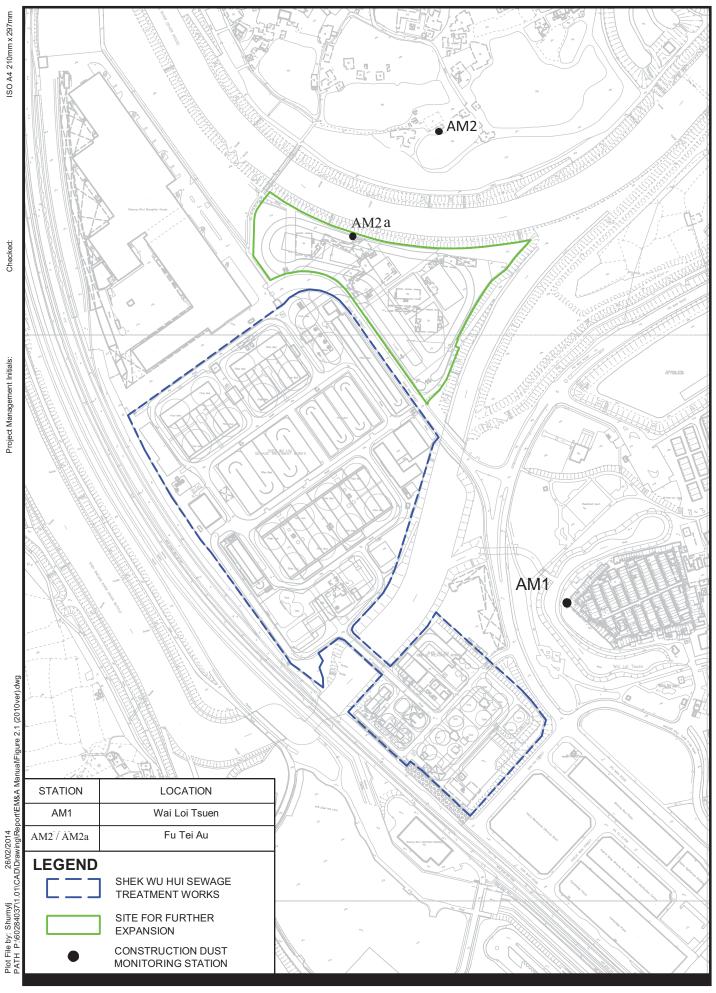

AGREEMENT NO. CE 40/2012 (DS) SHEK WU HUI SEWAGE TREATMENT WORKS - FURTHER EXPANSION PHASE 1A - INVESTIGATION PROPOSED CONSTRUCTION DUST MONITORING STATIONS FOR CONSTRUCTION PHASE AND OPERATION PHASE



Drawing No. 60284037/EM&AM/405

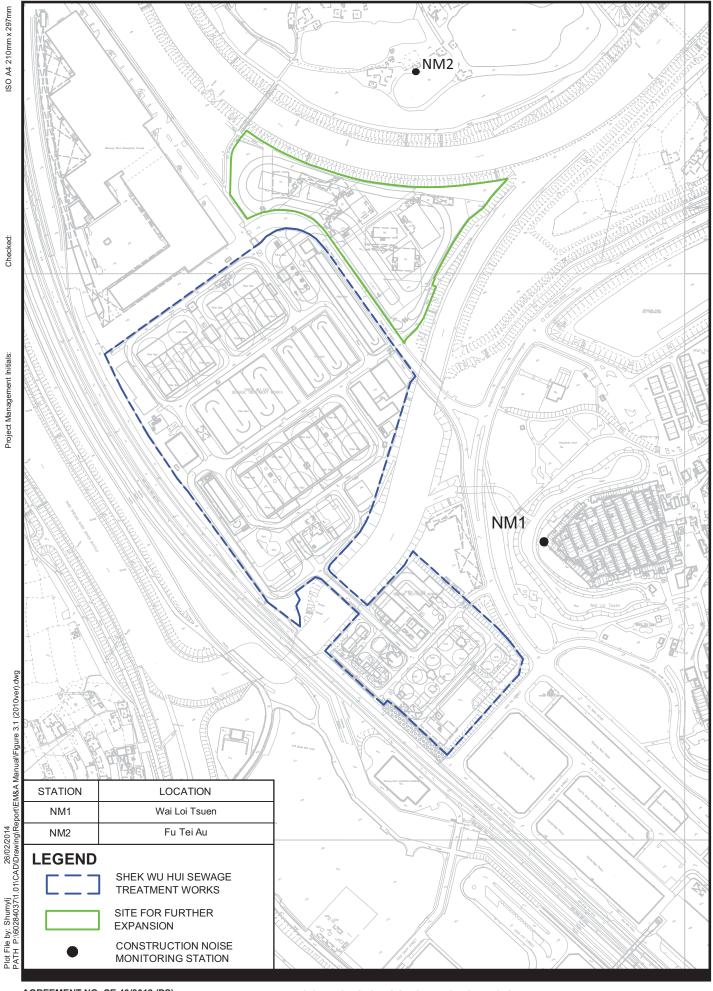

AGREEMENT NO. CE 40/2012 (DS) SHEK WU HUI SEWAGE TREATMENT WORKS - FURTHER EXPANSION PHASE 1A - INVESTIGATION

LOCATIONS OF CONSTRUCTION NOISE MONITORING STATIONS



Drawing No. 60284037/EM&AM/407

Project No.: 60284037 Date: FEB. 2014



Appendix F

EVENT ACTION PLAN

 $Z:\label{eq:label} Z:\label{eq:label} Z:\label{eq$

Event and Action Plan for Construction Dust

Trant		Action		
Event	ET	IEC	ER	Contractor
Action level being exceeded by one sampling	 Identify source, investigate the causes of complaint and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; Increase monitoring frequency to daily. 	 Check monitoring data submitted by ET; Check Contractor's working method. 	1. Notify Contractor.	 Rectify any unacceptable practice; Amend working methods if appropriate.
Action level being exceeded by two or more consecutive sampling	 Identify source; Inform IEC and ER; Advise the ER on the effectiveness of the proposed remedial measures; Repeat measurements to confirm findings; Increase monitoring frequency to daily; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with IEC and ER; If exceedance stops, cease additional monitoring. 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Supervise Implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Notify Contractor; Ensure remedial measures properly implemented. 	 Submit proposals for remedial actions to IEC within three working days of notification; Implement the agreed proposals; Amend proposal if appropriate.
Limit level being exceeded by one sampling	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform Contractor, IEC, ER, and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ER on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Notify Contractor; Ensure remedial measures properly implemented. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within three working days of notification; Implement the agreed proposals; Amend proposal if appropriate.
Limit level being exceeded by two or more consecutive sampling	 Notify IEC, ER, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. 	 Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within three working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated.

AUES



Event and Action Plan for Construction Noise

Event		Act	tion	
Event	ET	IEC	ER	Contractor
Action Level	 Notify IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, ER and Contractor; Discuss with the Contractor and formulate remedial measures; Increase monitoring frequency to check mitigation effectiveness. 	 Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented. 	 Submit noise mitigation proposals to IEC; Implement noise mitigation proposals.
Limit Level	 Identify source; Inform IEC, ER, EPD and Contractor; Repeat measurements to confirm findings; Increase monitoring frequency; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Inform IEC, ER and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. 	 Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated.



Appendix G

VALID CALIBRATION CERTIFICATES

 $Z:\label{eq:label} Z:\label{eq:label} Z:\label{eq$

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :			Tsuen						pration: 28-Ju			
Location]	D :	AM1				ľ			n Date: 28-A	-		
								ech	nician: K. C	. Cheung		
					C							
	Se	a Level I	Pressure	(hPa)		1007.5			Corrected P	Pressure (mn	n Hg)	755.625
			berature	` ´		29.1				erature (K)		302
		-					4		-			
				CA	LIB	RATIO	N ORIFICE					
				Make->	TIS	CH			Qstd S	lope ->	2.0	0411
				Model->	502	5A			Qstd Inter	cept ->	-0.	03059
				Serial # ->	161	2						
					С	ALIBR	ATION					
Plate	H20 (L)	H2O (R)	H20	Qstd		Ι	IC			LINEAR		
No.	(in)	(in)	(in)	(m3/min)	(c	hart)	corrected		R	EGRESSIO	N	
18	6.30	6.30	12.6	1.769		52	51.15			Slope = 24 .	0623	
13	5.10	5.10	10.2	1.593		47	46.23			ercept = 8.		
10	3.90	3.90	7.8	1.395		42	41.31		Corr. c	$\operatorname{coeff.} = 0.$	9990	
7 5	2.10	2.10	4.2 2.6	1.028		34	33.44					
5 1.30 1.30 2.6 0.812						28	27.54					
Calculations :									FLOW RAT	E CHART		
Qstd = 1/r	n[Sqrt(H	20(Pa/Ps	td)(Tstd	/Ta))-b]		60.0	00					
IC = I[Squ	t(Pa/Pstc	l)(Tstd/T	a)]						,	/ = 24.0623 x +	8 1803	
						50.0	00		,			
Qstd = sta												
IC = correction		-	es				10			ļ į		
I = actual		-				Actual chart response (IC) 30.05 20.05 20.02						
m = calibib = calibra	-	-	+			ŝuod				•		
	-	-		oration (deg	, K	e 30.0	00					
	-		_	ation (mm I	- 1	char			•			
1	press					20.0	00					
For subse	equent ca	alculatio	n of sam	pler flow:		Ă						
1/m((I)[S	Sqrt(298/	Tav)(Pav	r/760)]-b))								
						10.0	00					
m = samp	-											
b = samp		ept				0.0						
I = chart r	-	a ta					0.000				500	2.000
Tav = dail Pav = dail									Standard Flow	ivate (IIIo/MIN)		
r av – Uäll	y averag	e pressur	U									

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	RE'	s Site Of	fice				Date of Ca	alibration: 28-Jun	-16	
Location I	D :	AM2a				N	lext Calibra	tion Date: 28-Au	g-16	
							Te	echnician: K. C. (Cheung	
					С	ONDIT	IONS			
	Se	a Level I	Pressure	(hPa)	1	007.5		Corrected Pre	essure (mm F	Ig) 755.625
			erature	` ´	-	29.1			cature (K)	302
		Tomp	oratare			27.1		Temper		502
				CA	LIB	RATIO				
				Make->	TISC	CH		Qstd Slo	pe ->	2.00411
				Model->	5025	5A		Qstd Interce	ept ->	-0.03059
				Serial # ->	1612	2				
					C/	ALIBRA				
					0,					
Plate	H20 (L)	H2O (R)	H20	Qstd		Ι	IC]	LINEAR	
No.	(in)	(in)	(in)	(m3/min)	(cł	nart)	corrected		GRESSION	
18	6.10	6.10	12.2	1.741	· · ·	55	54.10		ope = 33.03	89
13	4.90	4.90	9.8	1.562		49	48.20		ept = -3.41	
10	3.80	3.80	7.6	1.378		43	42.29		eff. = 0.99	
7	2.40	2.40	4.8	1.098		33	32.46	000.00		20
5	1.50	1.50	3.0	0.871		26	25.57			
	1.50	1.50	5.0	0.071		20	23.31			
Calculations :								FLOW RATE	CHART	
Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b]						60.00	0			
IC = I[Sqr								у =	33.0389 x - 3.41	82
			L V			50.0	0			
Qstd = sta	ndard flo	w rate				50.00	0		1	
IC = correction			es							
I = actual		-	•••			<u>9</u> 40.0	0			
m = calibr		-				se (
b = calibra	-	-	t			uod				
	-	-		oration (deg	T V	2 30.00	0		· ·	
	-		_	ation (mm l		char				
PSIU = aCI	ual piess		ig canora		ng	Actual chart response (IC) 00.05 00.05 00.05				
For subse	auont c	alculatio	nofean	anlor flow:		1 20.00	0			
	-			-						
1/m((I)[S	oqri(298/	Tav)(Pav	///00)]-0))		10.0	0			
	1 1					10.0				
m = samp	-									
b = samp		ept				0.0	0			
I = chart r	-						0.000	0.500 1.000		2.000
Tav = dail		-						Standard Flow Ra	ate (m3/min)	
Pav = dail	y averag	e pressur	e							

ALS Technichem (HK) Pty Ltd ALS Laboratory Group ANALYTICAL CHEMISTRY & TESTING SERVICES SUB-CONTRACTING REPORT CONTACT WORK ORDER : MR BEN TAM HK1618617 CLIENT ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING RM A 20/F., GOLD KING IND BLDG, SUB-BATCH ADDRESS : 1 NO. 35-41 TAI LIN PAI ROAD, DATE RECEIVED 2-APR-2016 DATE OF ISSUE : 12-MAY-2016 KWAI CHUNG. N.T. HONG KONG PROJECT NO. OF SAMPLES : 1 CLIENT ORDER ----

General Comments

- Sample(s) were received in an ambient condition.
- Sample(s) analysed and reported on an as received basis.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatories	
Richard Fung	Rill
	1

General Manager

Position

This is the Final Report and supersedes any preliminary report with this batch number. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

> ALS Technichem (HK) Pty Ltd Part of the ALS Laboratory Group

11F. Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com WORK ORDER : HK1618617

: 1

SUB-BATCH CLIENT PROJECT

: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1618617-001	S/N: 366418	AIR	02-APR-2016	S/N: 366418

Equipment Verification Report (TSP)

Equipment Calibrated:

Туре:	Laser Dust monitor
Manufacturer:	Sibata LD-3B
Serial No.	366418
Equipment Ref:	EQ108
Job Order	HK1618617

Standard Equipment:

Standard Equipment:	Higher Volume Sampler
Location & Location ID:	AUES office (calibration room)
Equipment Ref:	HVS 018
Last Calibration Date:	22 Mar 2016

Equipment Verification Results:

Calibration Date:

3 April 2016

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr00min	10:15 ~ 12:15	23.0	1014.6	0.056	3126	26.1
2hr00min	12:20 ~ 14:20	23.0	1014.6	0.032	1688	14.1
2hr00min	14:25 ~ 16:25	23.0	1014.6	0.039	1707	14.2

Sensitivity Adjustment Scale Setting (Before Calibration) Sensitivity Adjustment Scale Setting (After Calibration)

677	(CPM)
679	(CPM)

Linear Regression of Y or X


Slope (K-factor):	0.0022	
Correlation Coefficient (R)	0.9864	
Date of Issue	6 April 2016	

Remarks:

1. Strong Correlation (R>0.8)

2. Factor 0.0022 should be apply for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment





TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Kwai Chung Location ID : Calibration Room					Date of Calibration: 22-Mar-16 Next Calibration Date: 22-Jun-16			
					С	OND	ITIONS	
Sea Level Pressure (hPa) Temperature (°C)					1013.4 16.6		Corrected Pressure (mm Hg) 760.05 Temperature (K) 290	
					CALIBI	RATI	ON ORIFIC	E
					TISC 5025 24-Mar	A		Qstd Slope ->2.10265Qstd Intercept ->-0.00335Expiry Date->24-Mar-16
					C	ALIBI	RATION	
Plate No.	H20 (L) (in)	H2O (R) (in)	H20 (in)	Qstd (m3/min)	I (char	rt)	IC corrected	LINEAR REGRESSION
18 13 10 8 5	4.2 3.2 2.4 1.6 1.1	4.2 3.2 2.4 1.6 1.1	8.4 6.4 4.8 3.2 2.2	1.400 1.222 1.059 0.865 0.717	57 52 47 42 35	e G	57.82 52.75 47.68 42.61 35.51	Slope = 31.6915 Intercept = 13.9178 Corr. coeff. = 0.9946
Pstd = acti	n[Sqrt(H t(Pa/Pstc ndard flo cted char chart res ator Qstd ator Qstd ator Qstd d temper ual press	d)(Tstd/T ow rate rt respond ponse d slope intercept ature dur ure durin	a)] es t ing calib g calibra n of san	pration (deg ation (mm I apler flow:	며, N Actual chart response (IC)	70.00 60.00 50.00 40.00 30.00 20.00		FLOW RATE CHART
m = sampler slope b = sampler intercept I = chart response Tav = daily average temperature Pav = daily average pressure					10.00 0.00 C		0.500 1.000 1.500 Standard Flow Rate (m3/min)	

ALS ALS L ANALYTICAL	ALS		
	SUB-CONTRACTING RE	PORT	
CONTACT	: MR BEN TAM	WORK ORDER	HK1618611
CLIENT	ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS	RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG	SUB-BATCH DATE RECEIVED DATE OF ISSUE	1 2-APR-2016 12-MAY-2016
PROJECT	:	NO. OF SAMPLES CLIENT ORDER	1

General Comments

- Sample(s) were received in an ambient condition.
- Sample(s) analysed and reported on an as received basis.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatori	es
Richard	Fung

General Manager

Position

This is the Final Report and supersedes any preliminary report with this batch number. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

> ALS Technichem (HK) Pty Ltd Part of the ALS Laboratory Group

11/F. Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com WORK ORDER

: HK1618611

SUB-BATCH CLIENT PROJECT

: 1 : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING :----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1618611-001	S/N: 366407	AIR	02-APR-2016 00:00	S/N: 366407

Equipment Verification Report (TSP)

Equipment Calibrated:

Туре:	Laser Dust monitor			
Manufacturer:	Sibata LD-3B			
Serial No.	366407			
Equipment Ref:	EQ107			
Job Order	HK1618611			

Standard Equipment:

Higher Volume Sampler
AUES office (calibration room)
HVS 018
22 Mar 2016

Equipment Verification Results:

Testing Date:

3 April 2016

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr00min	10:15 ~ 12:15	23.0	1014.6	0.056	3106	25.9
2hr00min	12:20 ~ 14:20	23.0	1014.6	0.032	1811	15.1
2hr00min	14:25 ~ 16:25	23.0	1014.6	0.039	1912	15.9

Sensitivity Adjustment Scale Setting (Before Calibration) Sensitivity Adjustment Scale Setting (After Calibration) 570 (CPM) 568 (CPM)

Linear Regression of Y or X


Slope (K-factor):	0.0022
Correlation Coefficient (R)	0.9955
Date of Issue	6 April 2016

Remarks:

1. Strong Correlation (R>0.8)

2. Factor 0.0022 should be apply for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment





TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :Gold King Industrial Building, Kwai ChungLocation ID :Calibration Room					Date of Calibration: 22-Mar-16 Next Calibration Date: 22-Jun-16		
			COND	ITIONS			
Sea Level Temj	Pressure perature	a second contract of the second se	1013.4 16.6		Corrected Pressure (mm Hg) 760.05 Temperature (K) 290		
		C	ALIBRATI	ON ORIFIC	E		
	Calibra	Make-> Model-> tion Date-> 2	TISCH 5025A 4-Mar-15		Qstd Slope ->2.10265Qstd Intercept ->-0.00335Expiry Date->24-Mar-16		
<i>c</i>			CALIB	RATION			
Plate H20 (L)H2O (R		Qstd	Ι	IC	LINEAR		
No. (in) (in)	(in)	(m3/min)	(chart)	corrected	REGRESSION		
18 4.2 4.2	8.4	1.400	57	57.82	Slope = 31.6915		
$\begin{array}{c ccccccccccccccccccccccccccccccccccc$	6.4	1.222	52	52.75	Intercept = 13.9178		
10 2.4 2.4	4.8	1.059	47	47.68	Corr. coeff. = 0.9946		
8 1.6 1.6 5 1.1 1.1	3.2 2.2	0.865 0.717	42 35	42.61 35.51			
Calculations : Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b] IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)] Qstd = standard flow rate IC = corrected chart respones I = actual chart response m = calibrator Qstd slope b = calibrator Qstd intercept Ta = actual temperature during calibration (deg K Pstd = actual pressure during calibration (mm Hg For subsequent calculation of sampler flow:					FLOW RATE CHART		
1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)							
m = sampler slope b = sampler intercept I = chart response				0.000	0.500 1.000 1.500		
av = daily average temper	ature e				Standard Flow Rate (m3/min)		

ALS L	ALS Technichem (HK) Ptų Ltd ALS Laboratorų Group ANALYTICAL CHEMISTRY & TESTING SERVICES				
	SUB-CONTRACTING RE	PORT			
CONTACT	: MR BEN TAM	WORK ORDER	HK1603561		
CLIENT ADDRESS	 ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD. 	SUB-BATCH DATE RECEIVED	: 1 : 21-JAN-2016		
PROJECT	KWAI CHUNG, N.T. HONG KONG	DATE OF ISSUE	25-JAN-2016		

General Comments

- Sample(s) were received in an ambient condition.
- Sample(s) analysed and reported on an as received basis.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories.

Position	
General Manager	

This is the Final Report and supersedes any preliminary report with this batch number. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd Part of the ALS Laboratory Group

11/F. Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com

10 11

WORK ORDER SUB-BATCH

CLIENT

PROJECT

: HK1603561 : 1

ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.	
HK1603561-001	S/N: 366410	AIR	21-JAN-2016	S/N: 366410	

Equipment Verification Report (TSP)

Equipment Calibrated:

Туре:	Laser Dust monitor
Manufacturer:	Sibata LD-3B
Serial No.	366410
Equipment Ref:	EQ110
Job Order	

Standard Equipment:

Standard Equipment:	Higher Volume Sampler
Location & Location ID:	AUES office (calibration room)
Equipment Ref:	HVS 018
Last Calibration Date:	2 January 2016
Equipment Ref:	HVS 018


Equipment Verification Results:

Testing Date:

4 to 6 January 2016

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr17min	17:30 ~ 19:47	20.6	1018.9	0.027	1566	11.4
2hr42min	17:00 ~ 19:42	20.7	1015.9	0.021	1422	8.7
2hr21min	18:00 ~ 20:21	20.9	1018.8	0.051	3318	23.4

Sensitivity Adjustment Scale Setting (Before Calibration) Sensitivity Adjustment Scale Setting (After Calibration)



Linear Regression of Y or X


Slope (K-factor):	0.0022
Correlation Coefficient	0.9986
Date of Issue	11 January 2016

Remarks:

1. **Strong** Correlation (R>0.8)

2. Factor 0.0022 should be apply for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment





TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Kwa Location ID : Calibration Room					ng, Kv	wai Ch	ung	Date of Calibration: 2-Jan-16 Next Calibration Date: 2-Apr-16
					(COND	TIONS	
	Sea Level Pressure (hPa) Temperature (°C)							Corrected Pressure (mm Hg) 766.5 Temperature (K) 292
					CALIE	BRATIO		CE
					TIS 502 24-M	5A		Qstd Slope -> 2.10265 Qstd Intercept -> -0.00335 Expiry Date-> 24-Mar-16
					C	CALIBR	RATION	
Plate		H2O (R)	H20	Qstd (m3/min)	I		IC	LINEAR
No. 18 13 10 8 5	(in) 4.1 3.2 2.4 1.6 1.0	(in) 4.1 3.2 2.4 1.6 1.0	(in) 8.2 6.4 4.8 3.2 2.0	(m3/min) 1.384 1.222 1.059 0.865 0.684	(cha 50 52 49 42 33	6 2 8 2	corrected 56.82 52.76 48.71 42.62 35.51	REGRESSION Slope = 30.1332 Intercept = 15.8637 Corr. coeff. = 0.9950
Calculations : Qstd = 1/m[Sqrt(H20(Pa/Pstd)(Tstd/Ta))-b] IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)] Qstd = standard flow rate IC = corrected chart respones I = actual chart response m = calibrator Qstd slope					00. 50. 50.	00	FLOW RATE CHART	
<pre>b = calibrator Qstd intercept Ta = actual temperature during calibration (deg K) Pstd = actual pressure during calibration (mm Hg) For subsequent calculation of sampler flow: 1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)</pre>				- ·	.04 Actual chart response 30. 20.	00		
b = samp I = chart r Tav = dail	m = sampler slope b = sampler intercept I = chart response Tav = daily average temperature Pav = daily average pressure					10.	00	0.500 1.000 1.500 Standard Flow Rate (m3/min)

ALS Technichem (HK) Pty Ltd

ALS Laboratory Group

ANALYTICAL CHEMISTRY & TESTING SERVICES



SUB-CONTRACTING	REPORT

CONTACT	: MR BEN TAM	WORK ORDER	HK1618634
CLIENT	ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS	RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG	SUB-BATCH DATE RECEIVED DATE OF ISSUE	1 2-APR-2016 12-MAY-2016
PROJECT		NO. OF SAMPLES CLIENT ORDER	1

General Comments

- Sample(s) were received in an ambient condition.
- Sample(s) analysed and reported on an as received basis.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories.

Signatories	()	Position	
Richard Fung	Killy	General Manager	
	X		

This is the Final Report and supersedes any preliminary report with this batch number. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd Part of the ALS Laboratory Group

11/F. Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com WORK ORDER SUB-BATCH

CLIENT

PROJECT

: HK1618634

: 1

: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING : -----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1618634-001	S/N: 456658	AIR	02-APR-2016	S/N: 456658

Equipment Calibrated:

Туре:	Laser Dust monitor
Manufacturer:	Sibata LD-3B
Serial No.	456658
Equipment Ref:	EQ115
Job Order	HK1618634

Standard Equipment:

Higher Volume Sampler
AUES office (calibration room)
HVS 018
22 Mar 2016

0.0022

0.9919

6 April 2016


Equipment Verification Results:

Calibration Date:

3 April 2016

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr00min	10:15 ~ 12:15	23.0	1014.6	0.056	3014	25.1
2hr00min	12:20 ~ 14:20	23.0	1014.6	0.032	1599	13.3
2hr00min	14:25 ~ 16:25	23.0	1014.6	0.039	1743	14.5

Sensitivity Adjustment Scale Setting (Before Calibration) Sensitivity Adjustment Scale Setting (After Calibration) 700 (CPM) 703 (CPM)



Remarks:

Date of Issue

Slope (K-factor):


1. **Strong** Correlation (R>0.8)

Linear Regression of Y or X

Correlation Coefficient (R)

2. Factor 0.0022 should be apply for TSP monitoring

*If R<0.5, repair or re-verification is required for the equipment



TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Location ID : Calibration Room					ıg, Kw	vai Ch	ung	Date of Calibration: 22-Mar-16 Next Calibration Date: 22-Jun-16
					(COND	ITIONS	
	Se	ea Level I Temp	Pressure perature	- diamana di Indiana di	10	013.4 16.6		Corrected Pressure (mm Hg) 760.05 Temperature (K) 290
					CALIE	BRATI	ON ORIFIC	E
Make-> TISCH Model-> 5025A Calibration Date-> 24-Mar-15								Qstd Slope -> 2.10265 Qstd Intercept -> -0.00335 Expiry Date-> 24-Mar-16
	ι. Έ				С	ALIB	RATION	
Plate No.	H20 (L) (in)	H2O (R) (in)	H20 (in)	Qstd (m3/min)	I (cha		IC corrected	LINEAR REGRESSION
18 13 10 8 5	4.2 3.2 2.4 1.6 1.1	4.2 3.2 2.4 1.6 1.1	8.4 6.4 4.8 3.2 2.2	1.400 1.222 1.059 0.865 0.717	57 57 47 47 42 35	7 2 7 2	57.82 52.75 47.68 42.61 35.51	Slope = 31.6915 Intercept = 13.9178 Corr. coeff. = 0.9946
Pstd = act For subse 1/m((I)[S	n[Sqrt(H rt(Pa/Psto ndard flo ected cha chart res rator Qsto ator Qsto ator Qsto al temper ual press equent co Sqrt(298/	d)(Tstd/T ow rate rt respond ponse d slope intercept ature dur ure durin	a)] es t ing calib g calibra n of san	pration (deg ation (mm I apler flow:		70.00 60.00 50.00 40.00 30.00 20.00		FLOW RATE CHART
m = sampler slope b = sampler intercept I = chart response Tav = daily average temperature Pav = daily average pressure					0.00 0	0.000	0.500 1.000 1.500 Standard Flow Rate (m3/min)	



Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C161796 證書編號

ITEM TESTED / 送檢环	頁目	(Job No./序引編號: IC16-0662)	Date of Receipt / 收件日期: 22 March 2016	
Description / 儀器名稱	:	Sound Level Meter (EQ015)		
Manufacturer / 製造商	:	Rion		
Model No. / 型號	:	NL-52		
Serial No. / 編號	:	00142581		
Supplied By / 委託者	:	Action-United Environmental Services and	Consulting	
		Unit A, 20/F., Gold King Industrial Buildin	ıg,	
		35-41 Tai Lin Pai Road, Kwai Chung, N.T.		

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C Line Voltage / 電壓 : ---

Relative Humidity / 相對濕度 : (55 ± 20)%

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 6 April 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only. The results do not exceed manufacturer's specification. The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By 測試

H T Wong Technical Officer

KC Lee Project Engineer

Certified By 核證 Date of Issue 簽發日期

:

7 April 2016

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 – 校正及檢測實驗所 c/o 香港新界屯門興安里一號青山灣機樓四樓 Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com



Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C161796 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration was performed before the test.
- 3. The results presented are the mean of 3 measurements at each calibration point.
- 4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C160077
CL281	Multifunction Acoustic Calibrator	PA160023

- 5. Test procedure : MA101N.
- 6. Results :
- 6.1 Sound Pressure Level
- 6.1.1 Reference Sound Pressure Level

	UUT Setting				Applied Value		IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L _A	А	Fast	94.00	1	94.4	± 1.1

6.1.2 Linearity

-	UU	Γ Setting	Applied	d Value	UUT	
Range	Function	Frequency	Time	Level	Freq.	Reading
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)
30 - 130	L _A	А	Fast	94.00	1	94.4 (Ref.)
	1107 214			104.00		104.4
				114.00		114.4

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

	UUT Setting			Applied Value		UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L _A	А	Fast	94.00	1	94.4	Ref.
			Slow			94.4	± 0.3

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 – 校正及檢測實驗所

c/o 香港新界屯門興安里一號青山灣機樓四樓



Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C161796 證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

ii worghting		Setting		Annl	ied Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _A	A	Fast	94.00	63 Hz	68.1	-26.2 ± 1.5
	2000				125 Hz	78.2	-16.1 ± 1.5
					250 Hz	85.7	-8.6 ± 1.4
					500 Hz	91.1	-3.2 ± 1.4
					1 kHz	94.4	Ref.
					2 kHz	95.6	$+1.2 \pm 1.6$
					4 kHz	95.4	$+1.0 \pm 1.6$
		- 			8 kHz	93.3	-1.1 (+2.1 ; -3.1)
					12.5 kHz	89.9	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

		Setting		Appli	ed Value	UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _C	С	Fast	94.00	63 Hz	93.5	-0.8 ± 1.5
					125 Hz	94.2	-0.2 ± 1.5
					250 Hz	94.3	0.0 ± 1.4
					500 Hz	94.4	0.0 ± 1.4
					1 kHz	94.4	Ref.
					2 kHz	94.2	-0.2 ± 1.6
					4 kHz	93.6	-0.8 ± 1.6
					8 kHz	91.4	-3.0 (+2.1 ; -3.1)
					12.5 kHz	88.0	-6.2 (+3.0 ; -6.0)

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 06015

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :	94 dB : 63 Hz - 125 Hz 250 Hz - 500 Hz 1 kHz 2 kHz - 4 kHz 8 kHz 12.5 kHz 104 dB : 1 kHz 114 dB : 1 kHz	
------------------------------------	--	--

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 – 校正及檢測實驗所

c/o 香港新界屯門興安里一號青山灣機樓四樓

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C162440 證書編號

ITEM TESTED / 送檢項目 Description / 儀器名稱 : Manufacturer / 製造商 : Model No. / 型號 : Serial No. / 編號 : Supplied By / 委託者 :	(Job No. / 序引編號: IC16-0843) Sound Level Meter (EQ011) Rion NL-52 01121362 Action-United Environmental Services an Unit A, 20/F., Gold King Industrial Build 35-41 Tai Lin Pai Road, Kwai Chung, N.	ing,
TEST CONDITIONS / 測記 Temperature / 溫度 : (2: Line Voltage / 電壓 :	$3 \pm 2)^{\circ}C$	Relative Humidity / 相對濕度 : (55 ± 20)%

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 10 May 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only. The results do not exceed manufacturer's specification. The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By 測試	:H T Wong Technical Officer		
Certified By 核證	: K C Lee Project Engineer	Date of Issue : 簽發日期	11 May 2016

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Certificate of Calibration 校正證書

Certificate No. : C162440 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration was performed before the test.
- 3. The results presented are the mean of 3 measurements at each calibration point.
- 4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C160077
CL281	Multifunction Acoustic Calibrator	PA160023

- 5. Test procedure : MA101N.
- 6. Results :
- 6.1 Sound Pressure Level
- 6.1.1 Reference Sound Pressure Level

	UUT	Setting		Applie	d Value	UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L _A	А	Fast	94.00	1	93.3	± 1.1

6.1.2 Linearity

UUT Setting			Applied Value		UUT	
Range	Function	Frequency	Time	Level	Freq.	Reading
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)
30 - 130	L _A	A	Fast	94.00	1	93.3 (Ref.)
				104.00		103.3
				114.00		113.3

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting			Applie	d Value	UUT	IEC 61672	
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
30 - 130	L _A	А	Fast	94.00	1	93.3	Ref.
			Slow			93.3	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



輝創工程有限公司

Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C162440 證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

A-weighting	8						
UUT Setting			Applied Value		UUT	IEC 61672	
Range	Function	Frequency	Time	Level	Freq.	Reading (dB)	Class 1 Spec. (dB)
(dB)		Weighting	Weighting	(dB)			
30 - 130	LA	A	Fast	94.00	63 Hz	67.0	-26.2 ± 1.5
					125 Hz	77.1	-16.1 ± 1.5
					250 Hz	84.6	-8.6 ± 1.4
					500 Hz	90.1	-3.2 ± 1.4
					1 kHz	93.3	Ref.
					2 kHz	94.5	$+1.2 \pm 1.6$
					4 kHz	94.3	$+1.0 \pm 1.6$
					8 kHz	92.3	-1.1 (+2.1 ; -3.1)
					12.5 kHz	88.9	-4.3 (+3.0 ; -6.0)
				h			

6.3.2 C-Weighting

C Heighting							XTC (1(20
	UUT Setting			Applied Value		UUT	IEC 61672
Range	Function	Frequency	Time	Level	Freq.	Reading	Class 1 Spec.
(dB)		Weighting	Weighting	(dB)	-	(dB)	(dB)
30 - 130	L _C	C	Fast	94.00	63 Hz	92.5	-0.8 ± 1.5
	C				125 Hz	93.1	-0.2 ± 1.5
					250 Hz	93.3	0.0 ± 1.4
					500 Hz	93.3	0.0 ± 1.4
					1 kHz	93.3	Ref.
					2 kHz	93.1	-0.2 ± 1.6
					4 kHz	92.5	-0.8 ± 1.6
					8 kHz	90.4	-3.0 (+2.1 ; -3.1)
					12.5 kHz	86.9	-6.2 (+3.0 ; -6.0)

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 07549

- Mfr's Spec. : IEC 61672 Class 1

10	2 kHz - 4 kHz 8 kHz 12.5 kHz 04 dB : 1 kHz	
----	---	--

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



輝創工程有限公司

Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C164098 證書編號

ITEM TESTED / 送檢項目		(Job No. / 序引編號:IC16-0843)	Date of Receipt / 收件日期: 15 July 2016		
Description / 儀器名稱	:	Sound Level Calibrator (EQ085)			
Manufacturer / 製造商	:	Rion			
Model No. / 型號	:	NC-73			
Serial No. / 編號	:	10655561			
Supplied By / 委託者	:	Action-United Environmental Services and C	Consulting		
		Unit A, 20/F., Gold King Industrial Building,			
	35-41 Tai Lin Pai Road, Kwai Chung, N.T.				
TEST CONDITIONS / 測試條件					

Temperature / 溫度 : (23 ± 2)°C Line Voltage / 電壓 : --- Relative Humidity / 相對濕度 : (55 ± 20)%

TEST SPECIFICATIONS / 測試規範

Calibration

DATE OF TEST / 測試日期 : 27 July 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification & user's specified acceptance criteria. (after adjustment) The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By 測試	:H T Wong Technical Officer		
Certified By 核證	: KOLee Project Engineer	Date of Issue : 簽發日期	28 July 2016

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory c/o 4F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 – 校正及檢測實驗所 c/o 香港新昇屯門興安里一號青山灣機樓四樓 Tel電話: 2927 2606 Fax/博真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com



Certificate of Calibration 校正證書

Certificate No. : C164098 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- 2. The results presented are the mean of 3 measurements at each calibration point.
- 3. Test equipment :

Equipment ID CL130 CL281 TST150A

<u>Description</u> Universal Counter Multifunction Acoustic Calibrator Measuring Amplifier <u>Certificate No.</u> C163709 PA160023 C161175

- 4. Test procedure : MA100N.
- 5. Results :
- 5.1 Sound Level Accuracy

5.1.1 Before Adjustment

UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	* 93.4	± 0.5	± 0.2

* Out of Mfr's Spec.

5.1.2 After Adjustment

UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	94.0	± 0.5	± 0.2

5.2 Frequency Accuracy

5.2.1 Before Adjustment

UUT Nominal Value	Measured Value	User's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	0.955	1 kHz ± 6 %	± 1

5.2.2 After Adjustment

	UUT Nominal Value	Measured Value	User's	Uncertainty of Measured Value
	(kHz)	(kHz)	Spec.	(Hz)
	1	0.954	1 kHz ± 6 %	± 1

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Certificate of Calibration 校正證書

Certificate No.: C164098 證書編號

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



輝創工程有限公司

Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No. : C162125 證書編號

Unit A, 20/F., Gol	
TEST CONDITIONS / 測試條件 Temperature / 溫度 : (23 ± 2)°C Line Voltage / 電壓 :	Relative Humidity / 相對濕度 : (55 ± 20)%
TEST SPECIFICATIONS / 測試規範 Calibration check DATE OF TEST / 測試日期 : 22 April 2	2016
TEST RESULTS / 測試結果 The results apply to the particular unit-under-test The results do not exceed manufacturer's specific The results are detailed in the subsequent page(s) The test equipment used for calibration are trace - The Government of The Hong Kong Special A - Agilent Technologies / Keysight Technologies - Rohde & Schwarz Laboratory, Germany - Fluke Everett Service Center, USA	cation.). able to National Standards via : .dministrative Region Standard & Calibration Laboratory
Tested By : Worf[. 測試 H T Wong	

Certified By 核證

Date of Issue : 簽發日期

25 April 2016

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory. 本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

:

Sun Creation Engineering Limited – Calibration & Testing Laboratory c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 – 校正及檢測實驗所 c/o 香港新界屯門興安里一號青山灣機樓四樓 Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

Technical Officer

K C/Lee Project Engineer



Certificate of Calibration 校正證書

Certificate No. : C162125 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- 2. The results presented are the mean of 3 measurements at each calibration point.
- 3. Test equipment :

<u>Equipment ID</u> CL130	<u>Description</u> Universal Counter	<u>Certificate No.</u> C153519
CL281	Multifunction Acoustic Calibrator	PA160023
TST150A	Measuring Amplifier	C161175

- 4. Test procedure : MA100N.
- 5. Results :
- 5.1 Sound Level Accuracy

UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.1		

5.2 Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value				
(kHz)	(kHz)	Spec.	(Hz)				
1	1.000 0	1 kHz ± 0.1 %	± 0.1				

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Appendix H

IMPACT MONITORING SCHEDULE

 $Z: \label{eq:loss} 2015 \ (Shek Wu Hui) \ (600 \ EM\&A Report \ Impact \ Monthly EM\&A Report \ 11 th EM\&A \ (August \ 2016) \ R0054v \ 2.doc \ 2$



Impact Monitoring Schedule for Reporting Month – August 2016

		Dust Mo	onitoring	
	Date	1-hour TSP	24-hour TSP	Noise Monitoring
Mon	1-AUG-16	\checkmark		\checkmark
TUE	2-AUG-16			
WED	3-AUG-16			
THU	4-AUG-16		√	
Fri	5-AUG-16			
SAT	6-AUG-16	\checkmark		
SUN	7-AUG-16			
Mon	8-AUG-16			
TUE	9-AUG-16			
WED	10-AUG-16		✓	
THU	11-AUG-16			
Fri	12-AUG-16	\checkmark	*	√
SAT	13-AUG-16			
SUN	14-AUG-16			
Mon	15-AUG-16			
TUE	16-AUG-16		✓	
WED	17-AUG-16			
THU	18-AUG-16	\checkmark		\checkmark
Fri	19-AUG-16			
SAT	20-AUG-16			
SUN	21-AUG-16			
Mon	22-AUG-16		✓	
TUE	23-AUG-16			
WED	24-AUG-16	\checkmark		\checkmark
THU	25-AUG-16			
Fri	26-AUG-16			
SAT	27-AUG-16		√	
SUN	28-AUG-16			
Mon	29-AUG-16			
TUE	30-AUG-16	\checkmark		\checkmark
WED	31-AUG-16			

*Additional 24-Hour Air Monitoring at AM1

✓	Monitoring Day
	Sunday or Public Holiday

Monitoring Location

Air Quality	1-hour TSP	AM1 and AM2
	24-hour TSP	AM1 and AM2a
Construction N	oise	NM1 and NM2



Impact Monitoring Schedule for next Reporting Period – September 2016

		Dust Mo		
	Date	1-hour TSP	24-hour TSP	- Noise Monitoring
THU	1-Sep-16			
Fri	2-SEP-16		✓	
SAT	3-SEP-16			
SUN	4-SEP-16			
Mon	5-SEP-16	\checkmark		\checkmark
TUE	6-SEP-16			
WED	7-Sep-16			
Thu	8-SEP-16		\checkmark	
Fri	9-SEP-16			
SAT	10-SEP-16	\checkmark		
SUN	11-SEP-16			
Mon	12-SEP-16			
TUE	13-SEP-16			
WED	14-Sep-16		✓	
Thu	15-SEP-16	\checkmark		\checkmark
Fri	16-Sep-16			
SAT	17-Sep-16			
SUN	18-SEP-16			
Mon	19-SEP-16			
TUE	20-Sep-16		✓	
WED	21-Sep-16	\checkmark		\checkmark
THU	22-SEP-16			
Fri	23-SEP-16			
SAT	24-SEP-16			
SUN	25-SEP-16			
Mon	26-SEP-16		✓	
TUE	27-SEP-16	\checkmark		\checkmark
WED	28-SEP-16			
THU	29-SEP-16			
Fri	30-SEP-16		\checkmark	

\checkmark	Monitoring Day
	Sunday or Public Holiday

Monitoring Location

Air Quality	1-hour TSP	AM1 and AM2
	24-hour TSP	AM1 and AM2a
Construction N	oise	NM1 and NM2



Appendix I

24-HOUR TSP AND CONSTRUCTION NOISE MONITORING DATA



24-Hr TSP Monitoring Data for AM1

DATE	SAMPLE	ELAPSED TIME		CHART READING			AVG TEMP	AVG AIR PRESS	STANDARD FLOW RATE	AIR VOLUME	FILTER	WEIGHT g)	DUST WEIGHT COLLECTED	24-Hr TSP	
	NUMBER	INITIAL	FINAL	(min)	MIN	MIN MAX AVG		(°C)	(hPa)	(m ³ /min)	(std m ³)	INITIAL	FINAL	(g)	$(\mu g/m^3)$
4-Aug-16	29771	14459.40	14483.37	1438.20	24	24	24.0	26.9	1008.7	0.65	938	2.8015	2.8355	0.0340	36
12-Aug-16	29853	14496.39	14520.28	1433.40	26	27	26.5	28.1	1001.3	0.75	1074	2.8531	2.9057	0.0526	49
16-Aug-16	29863	14520.28	14544.28	1440.00	24	26	25.0	28.4	1005.5	0.69	992	2.8005	2.8350	0.0345	35
22-Aug-16	29897	14544.28	14568.28	1440.00	23	26	24.5	28.5	1005.5	0.67	962	2.8193	2.8501	0.0308	32
27-Aug-16	29883	14568.28	14592.28	1440.00	27	28	27.5	28.4	1006.1	0.79	1141	2.8057 2.9012		0.0955	84
24-Hr TSP M	lonitoring Da	nta for AM2	2a												
DATE	SAMPLE	ELAPSED TIME			CHART READING			AVG TEMP	AVG AIR PRESS	STANDARD FLOW RATE	AIR VOLUME	FILTER WEIGHT		DUST WEIGHT COLLECTED	24-Hr TSP
	NUMBER	INITIAL	FINAL	(min)	MIN	MAX	AVG	(°C)	(hPa)	(m ³ /min)	(std m ³)	INITIAL	FINAL	(g)	$(\mu g/m^3)$
4-Aug-16	29772	11032.35	11056.34	1439.40	32	32	32.0	26.9	1008.7	1.07	1535	2.7948	2.8238	0.0290	19
10-Aug-16	29791	11056.34	11080.30	1437.60	38	43	40.5	28.7	1004.6	1.32	1893	2.8071	2.8604	0.0533	28
16-Aug-16	29854	11080.30	11104.30	1440.00	37	40	38.5	28.4	1005.5	1.26	1811	2.8633	2.9042	0.0409	23
22-Aug-16	29862	11104.30	11128.31	1440.60	39	42	40.5	28.5	1005.5	1.32	1898	2.7950	2.8323	0.0373	20
27-Aug-16	29898	11128.31	11152.31	1440.00	40	45	42.5	28.4	1006.1	1.38	1984	2.8256	2.8796	0.0540	27

Noise Measu	oise Measurement Results (dB) of NM1																			
Date	Start Time	1 st Leq _{5min}	L10	L90	2 nd Leq _{5min}	L10	L90	3 nd Leq _{5min}	L10	L90	4 th Leq _{5min}	L10	L90	5 th Leq _{5min}	L10	L90	6 th Leq _{5min}	L10	L90	Leq30min
1-Aug-16	9:30	51.8	55.0	44.4	51.8	54.8	42.9	51.6	54.8	43.2	52.8	56.5	44.6	52.0	55.5	44.2	52.6	55.8	44.8	52
12-Aug-16	9:39	55.4	57.9	51.7	55.5	58.2	52.2	54.6	56.5	51.0	55.4	58.7	50.4	57.6	60.4	51.6	55.9	58.8	51.5	56
18-Aug-16	10:18	55.2	58.3	52.1	53.0	56.1	51.1	54.5	56.9	51.6	54.6	57.1	51.5	55.9	58.0	52.8	56.9	59.2	52.8	55
24-Aug-16	9:39	55.1	58.5	51.1	54.4	57.2	50.2	46.0	58.5	51.3	57.7	60.6	51.0	57.8	59.1	51.2	56.5	58.7	51.4	56
30-Aug-16	9:41	56.8	59.8	48.2	57.5	59.9	51.5	55.3	58.7	49.0	53.9	57.4	48.4	56.6	60.4	52.6	55.2	58.4	51.4	56
Noise Measu	irement	t Results	(dB) of	NM2																
Date	Start Time	1 st Leq _{5min}	L10	L90	2 nd Leq _{5min}	L10	L90	3 nd Leq _{5min}	L10	L90	4 th Leq _{5min}	L10	L90	5 th Leq _{5min}	L10	L90	6 th Leq _{5min}	L10	L90	Leq30min
1-Aug-16	10:30	51.1	53.4	46.4	51.8	54.3	46.7	53.2	55.6	45.0	51.5	54.6	44.8	50.9	53.7	45.0	50.9	54.0	45.2	52
12-Aug-16	13:48	53.6	56.2	47.5	52.7	55.4	47.5	53.8	54.9	47.2	47.7	50.5	46.1	49.8	50.3	46.5	46.6	49.8	45.7	52
18-Aug-16	13:36	50.0	51.9	44.9	50.9	53.5	45.4	49.2	51.7	45.3	47.5	49.5	44.2	46.7	48.9	45.1	44.6	47.4	44.8	49
24-Aug-16	13:41	49.4	51.9	45.7	50.5	53.2	47.2	51.6	54.5	48.0	47.0	50.9	44.6	49.6	51.2	44.3	46.0	49.9	45.6	49
30-Aug-16	13:21	48.2	50.2	45.5	47.6	49.3	44.8	51.8	53.9	46.7	49.8	51.2	46.3	48.2	50.7	47.2	50.5	51.1	45.6	50




Appendix J


GRAPHICAL PLOTS

 $Z:\label{eq:label} Z:\label{eq:label} Z:\label{eq$




<u>Air Quality – 24-Hour TSP</u>

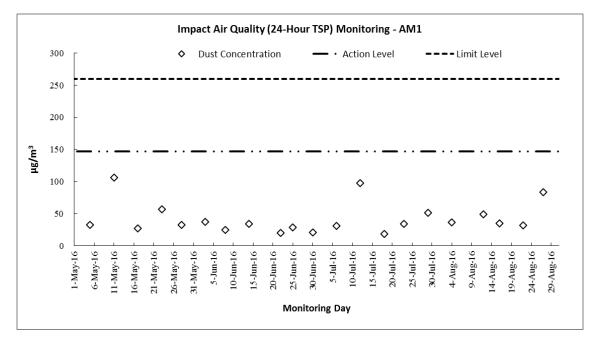

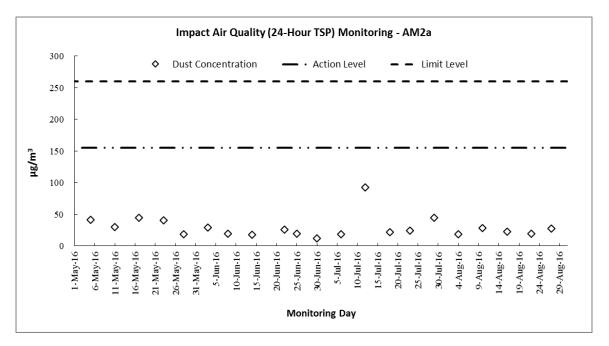




<u>Air Quality – 1-Hour TSP</u>

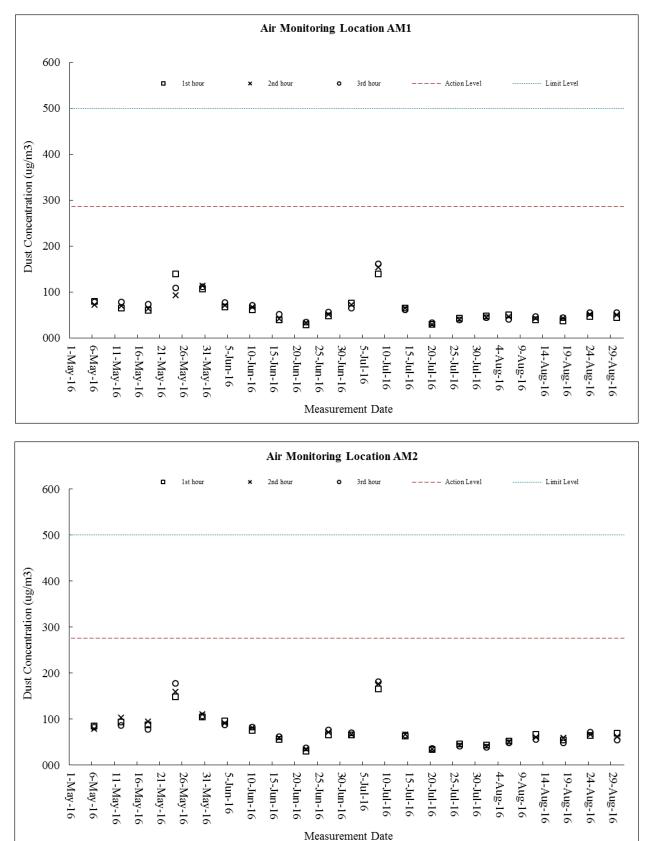

×

×



×

×

×

Leq30min

Noise Monitoring Location NM1

×

---- Limit Level

_ _ _ _ _ _

×

×

×



×

29-Aug-16

×

×

×

Construction Noise

80

75

70

65

60

55

50


45

×

×

Noise Level (dB(A))

DSD Contract No: DC/2013/09

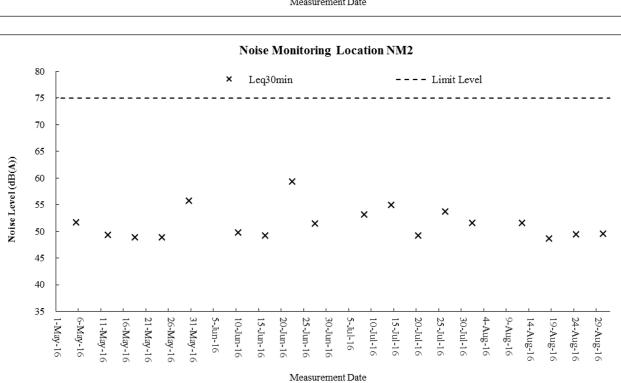



Appendix K

METEOROLOGICAL DATA DURING THE REPORTING MONTH (TA KWU LING STATION)



				,	Ta Kwu I	Ling Station	
Date		Weather	Total Rainfall (mm)	Mean Air Temp. (°C)	Wind Speed (km/h)	Mean Relative Humidity (%)	Wind Directio n
1-Aug-16	Mon	Very hot during the day	4.6	29	7.6	79.2	S/SW
2-Aug-16	Tue	Mainly fine apart from isolated showers.	12.1	26.6	19.5	86	S/SE
3-Aug-16	Wed	Light to moderate southwesterly winds.	17.3	27.1	6	89.7	E/NE
4-Aug-16	Thu	Very hot during the day	20.9	27.9	7.7	87.2	E/NE
5-Aug-16	Fri	Mainly fine apart from isolated showers.	Trace	29.2	4.9	80	E/NE
6-Aug-16	Sat	Very hot with sunny periods.	0	29.8	5.3	81	E/SE
7-Aug-16	Sun	Very hot with sunny periods.	0	30.7	9.5	83	E/SE
8-Aug-16	Mon	Very hot with sunny periods.	0	31	7.5	73.5	S/SW
9-Aug-16	Tue	Very hot with sunny periods.	33.5	29.4	11.9	81.7	W/NW
10-Aug-16	Wed	Mainly cloudy with a few showers. Light winds.	39.8	26.1	4.5	90.7	E/SE
11-Aug-16	Thu	Mainly cloudy with a few showers. Light winds.	42.1	28.5	4.9	83.2	S/SE
12-Aug-16 13-Aug-16	Fri Sat	Very hot with sunny periods. Sunny intervals in the afternoon. Mainly cloudy	0.4 Trace	27.5 29.3	4.1 5.1	83.5 85	S/SW E/NE
-		tonight					
14-Aug-16	Sun	Moderate east to southeasterly winds. Sunny intervals in the afternoon. Mainly cloudy	25.7	27.3	7.5	87.5	E/NE
15-Aug-16	Mon	tonight	19.1	27.8	4.5	83.7	N/NW
16-Aug-16	Tue	Sunny intervals in the afternoon. Mainly cloudy tonight	49.9	27	4.5	89	S/SE
17-Aug-16	Wed	Sunny intervals in the afternoon. Mainly cloudy tonight	40.9	27.3	12.5	89	E/NE
18-Aug-16	Thu	Moderate east to southeasterly winds.	50.9	27.8	12.6	87.5	E/NE
19-Aug-16	Fri	Sunny intervals in the afternoon. Mainly cloudy tonight	10.5	29	7.9	83.5	E/NE
20-Aug-16	Sat	Very hot with sunny periods.	3.8	30	6	82	S/Sw
21-Aug-16	Sun	Sunny intervals in the afternoon. Mainly cloudy tonight	39.9	27.7	4.1	81	S/SW
22-Aug-16	Mon	Sunny intervals in the afternoon. Mainly cloudy tonight	0	29.4	6.1	76.2	E/NE
23-Aug-16	Tue	Sunny intervals in the afternoon. Mainly cloudy tonight	0	29.9	5.3	72.7	S/SE
24-Aug-16	Wed	Moderate east to southeasterly winds.	0	30.5	5	76.3	S/SE
25-Aug-16	Thu	Sunny intervals in the afternoon. Mainly cloudy tonight	0	30.1	4.4	78.1	S/SW
26-Aug-16	Fri	Very hot with sunny periods.	0	30.5	4.6	74.5	S/SW
27-Aug-16	Sat	Sunny intervals in the afternoon. Mainly cloudy tonight	3.5	29.4	6.5	75.3	Ν
28-Aug-16	Sun	Mainly cloudy with isolated showers.	8.7	27.9	7	74.2	N
29-Aug-16	Mon	Mainly cloudy with isolated showers.	Trace	26	7	70	E/NE
30-Aug-16	Tue	Dry with sunny periods in the afternoon.	0	27.5	4.5	74.5	N/NW
31-Aug-16	Wed	Mainly cloudy with showers and a few squally thunderstorms.	0.2	27.9	3.5	75.5	S/SW



Appendix L

MONTHLY SUMMARY WASTE FLOW TABLE

 $Z:\label{eq:label} Z:\label{eq:label} Z:\label{eq$

Appendix C

Monthly Summary Waste Flow Table

Department:	Drainage Services Department	Contract No.:	DC/2013/09		
Contract Title:	Advance Works for Shek Wu	Hui Sewage Treatment Works - Fu	urther Expansion Phase 1	A and Sewerage Works at P	ing Che Road
Commencement Date	: 21-Jul-2015	Estimated completion Date:	19-Aug-2016	Estimated Contract Sum:	1.56M

		Actual Quanti	ities of Inert C&D I	Materials Generated	Monthly			Actual Quantities	of C&D Waste	s Generated Month	ly
Month	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan	0.335	0.111	0.060	0.000	0.164	0.000	0.000	0.000	0.000	0.000	0.000
Feb	2.377	0.089	0.050	2.228	0.010	0.000	0.000	0.000	0.000	0.000	0.008
Mar	0.141	0.015	0.050	0.000	0.076	0.000	0.000	0.000	0.000	0.000	0.007
Apr	0.160	0.010	0.050	0.000	0.100	0.000	0.000	0.000	0.000	0.000	0.023
May	0.334	0.000	0.010	0.000	0.324	0.000	0.000	0.000	0.000	0.000	0.026
June	2.517	0.024	0.300	0.000	2.193	0.000	0.000	0.000	0.000	0.000	0.013
Sub-total	5.863	0.249	0.520	2.228	2.866	0.000	0.000	0.000	0.000	0.000	0.076
July	3.284	0.000	0.150	0.000	3.134	0.000	0.000	0.000	0.000	0.000	0.002
Aug	0.396	0.005	0.100	0.000	0.291	0.000	4.720	0.000	0.000	0.000	0.012
Sep											
Oct											
Nov											
Dec											
Total	9.543	0.254	0.770	2.228	6.291	0.000	4.720	0.000	0.000	0.000	0.090

Notes: (1) The waste flow table should cover the whole construction period of the Contract.

(2) The original estimates of the C&D materials should be the estimates at contract commencement and should not be altered during construction.

(3) Inert C&D materials that are specified in the Contract to be imported for use at the Site shall be separately indicated.

(4) The yearly estimates of the C&D materials should be updated as appropriate taking into account the latest works programme etc.

(5) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.



Appendix M

IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)

 $Z:\label{eq:label} Z:\label{eq:label} Z:\label{eq$

-	y Environmental Monuoring and Audu (EM&A) Report for August 20.			-		
EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
Air Qualit	y Impact					
S2.4.1.3	 Dust suppression measures stipulated in the Air Pollution Control (Construction Dust) Regulation and good site practices: Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; Any dusty material remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; A stockpile of dusty material should not be extended beyond the pedestrian barriers, fencing or traffic cones; The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle; Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores; When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period. The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials; Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; 	To minimize the dust impact	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Air Pollution Control Ordinance (APCO) and Air Pollution Control (Construction Dust) Regulation



EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
Air Qualit	ty Impact					
	 Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding; Any skip hoist for material transport should be totally enclosed by impervious sheeting; Every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides; Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed; Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system; and Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabilizer within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies. 					

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
Noise Imp	pact					
\$3.4.1.1	Use of movable barrier, enclosure, acoustic mat and quiet plant. Use of wooden frames barrier with a small-cantilevered upper portion of superficial density not less than 14kg/m ² on a skid footing with 25mm thick internal sound absorptive lining.	To minimize construction noise impact arising from the Project at the affected noise sensitive receivers (NSRs)	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM, Noise Control Ordinance (NCO)
\$3.4.1.2	 Good Site Practice: Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program. Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program. Mobile plant, if any, should be sited as far away from NSRs as possible. Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum. Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities. 	To minimize construction noise impact arising from the Project at the affected NSRs	Contractor	Work Sites	Construction period of Advance Works and Main Works of Phase 1A	EIAO-TM, NCO

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
Ecologica						
\$4.2.1.1	Solid dull green noise/visual barriers of at least 2m high shall be erected and maintained between active works area and all areas of ecological importance.	Minimize noise and human disturbances during construction phase.	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM
\$4.2.1.2	Avoid unnecessary lighting.	Minimize mortality impacts on birds.	Design / Contractor/ Plant Operator	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM
\$4.2.1.3	Good construction site practice to minimise dust generation should be followed on all construction sites. Measures to avoid, minimise and mitigate impacts on air quality are detailed in this schedule	Minimize dust generation from construction sites.	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM
S4.2.1.4	 The following measures to avoid, minimise and mitigate impact on water quality during construction phase shall be implemented Temporary sewerage and drainage to be designed and installed to collect wastewater and prevent it from entering water bodies; Proper locations well away from nearby water bodies should be used for temporary storage of materials (i.e. equipment, filling materials, chemicals and fuel) and temporary stockpiles of construction debris and spoil, and these should be identified before commencement of works; To prevent muddy water entering nearby water bodies, work sites close to nearby water bodies should be isolated, using such items as sandbags or silt curtains with lead edge at bottom and properly supported props. Other protective measures should also be taken to ensure that no pollution or siltation occurs to the water gathering grounds of the work sites; Construction debris and spoil should be covered and/or properly disposed of as soon as possible to avoid these being washed into nearby water bodies; Proper locations for discharge outlets of temporary wastewater treatment facilities well away from sensitive receivers should be identified; 	Avoid, minimise and mitigate impact on water quality	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM



EM&A		Objectives of the Recommended	Who to	Location of	When to	What requirements
Ref.	Recommended Mitigation Measures	Measures & Main Concern to	implement the measures?	the measure	implement the measures?	or standards for the measure to achieve
		Address				
Ecologica						Γ
	• Adequate lateral support should be erected where necessary in					
	order to prevent soil/mud from slipping into water bodies;Site boundaries should be clearly marked and any works beyond					
	the boundary strictly prohibited;					
	• Regular water monitoring and site audit should be carried out at					
	adequate points along any watercourses where construction works					
	are underway upstream within their catchments and also on the Ng					
	Tung, Sheung Yue and Shek Sheung Rivers. If the monitoring and					
	audit results show that pollution occurs, adequate measures including temporarily cessation of works should be considered;					
	 Excavation profiles should be properly designed and executed with 					
	attention to the relevant requirements for environment, health and					
	safety;					
	• Where soil to be excavated is situated beneath the groundwater					
	table, it may be necessary to lower the groundwater table by					
	installing well points or similar means;					
	• Stockpiling sites should be lined with impermeable sheeting and					
	bunded. Stockpiles should be properly covered by impermeable					
	sheeting to reduce dust emission during dry season or contaminated run-off during rainy season. Watering should be avoided on					
	stockpiles of contaminated soil to minimize contaminated runoff					
	and construction materials should be properly covered and located					
	away from nearby water bodies; and					
	• Supply of suitable clean backfill material after excavation, if					
	required.					
	• Vehicles containing any excavated materials should be suitably					
	covered to limit potential dust emissions or contaminated run-off,					
	and truck bodies and tailgates should be sealed to prevent discharge during transport or during wet season;					
	 Speed control for the trucks carrying contaminated materials should 					
	be enforced;					
	• Vehicle wheel washing facilities at construction sites' exit points					
	should be established and used, where necessary; and					
	• Other measures as detailed in this schedule.					

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
Water Qu	ality Impact					
S5.2.2.1	Construction Site Runoff Practices and measures provided in the Practice Note for Professional Persons on Construction Site Drainage, (PROPECC PN1/94) should be followed where applicable.	Control construction runoff	Contractors	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM, WPCO, EIAO
\$5.2.2.2 55.2.2.3	 Sewage from Workforce Portable chemical toilets and sewage holding tanks should be provided for handling the construction sewage generated by the workforce. A licensed Contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project. Regular environmental audit on construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site. It is anticipated that sewage generation during the construction phase of the Project would not cause water quality impact after undertaking all required measures 	Handling of site sewage	Contractors	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	EIAO-TM, WPCO, EIAO

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
Waste Mar						
S6.2.2.1	 Good Site Practices and Waste Reduction Measures: Nomination of an approved person, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; Training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling; Provision of sufficient waste disposal points and regular collection for disposal; Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; An Environmental Management Plan (EMP) should be prepared by the contractor and submitted to the Engineer for approval. 	Minimize waste generation during construction	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Waste Disposal Ordinance (WDO)
\$6.2.3.1	 Waste Reduction Measures: Segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal; Proper storage and site practices to minimize the potential for damage and contamination of construction materials; Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste; Sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete, metal etc.); and Provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling. 	Reduce waste generation	Contractor	Work Sites	Prior to the commencement of construction of Advance Works and Main Works of Phase 1A	WDO
\$6.2.4.1 - \$6.2.4.2	 Storage, Collection and Transportation of Waste Should any temporary storage or stockpiling of waste is required, recommendations to minimize the impacts include: Waste, such as soil, should be handled and stored well to ensure secure 	Minimize waste impacts arising from waste storage	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	WDO

DSD Contract No: DC/2013/09 Advance Works for Shek Wu Hui Sewage Treatment Works – Further Expansion Phase 1A and Sewerage Works at Ping Che Road 11th Monthly Environmental Monitoring and Audit (EM&A) Report for August 2016



EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
Waste Ma	nagement					
	 containment, thus minimizing the potential of pollution; Stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; and Different locations should be designated to stockpile each material to enhance reuse. Remove waste in timely manner; Employ the trucks with cover or enclosed containers for waste transportation; Obtain relevant waste disposal permits from the appropriate authorities; and 					
	• Disposal of waste should be done at licensed waste disposal facilities.					
\$6.2.5.2	 C&D Materials from Site Formation Maintain temporary stockpiles and reuse excavated fill material for backfilling; Carry out on-site sorting; Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; Adopt "selective demolition" technique to demolish the existing structure and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible; and Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified. 	Minimize waste impacts from excavated and C&D materials	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Land (Miscellaneous Provisions) Ordinance, WDO, ETWB TCW No. 19/2005
\$6.2.5.3	 C&D Material from Buildings Demolition and New Building Construction The Contractor should recycle as much as possible of the C&DM on-site. Public fill and C&DM waste should be segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal. For example, concrete and masonry can be crushed and used as fill, and steel reinforcing bar can be used by scrap steel mills. Different areas of the work sites should be designated for such segregation and storage. The use of wooden hoardings shall not be allowed. An alternative material, such as metal, aluminium or alloy etc, could be used. Government has developed a charging policy for the disposal of waste to landfill at present. It will provide additional incentive to reduce the volume of generated waste and ensure proper segregation to allow 	Minimize waste impacts from building demolition and new building construction	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Land (Miscellaneous Provisions) Ordinance, WDO, ETWB TCW No. 19/2005

Z:\Jobs\2015\TCS00757 (Shek Wu Hui)\600\EM&A Report\Impact\Monthly EM&A Report\11 th EM&A (August 2016)\R0054v2.doc

DSD Contract No: DC/2013/09 Advance Works for Shek Wu Hui Sewage Treatment Works – Further Expansion Phase 1A and Sewerage Works at Ping Che Road 11th Monthly Environmental Monitoring and Audit (EM&A) Report for August 2016



EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
Waste Ma	nagement					
	 reuse of the inert material on site when implemented. In order to minimize the impacts of the demolition works, the generated wastes must be cleared as quickly as possible after demolition. Therefore, the demolition and clearance works should be undertaken simultaneously. To facilitate proper segregation of inert and non-inert C&D material arising from demolition works, selective demolition method should be adopted. 					
S6.2.5.4	 Chemical Waste If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producers. Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste contractor. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation 	Control the chemical waste and ensure proper storage, handling and disposal	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Waste Disposal (Chemical Waste General) Regulation, Code of Practice on the Packaging, Labelling and Storage of Chemical Waste
\$6.2.5.5	 General Refuse General refuse should be stored in enclosed bins separately from construction and chemical wastes. Recycling bins should also be placed to encourage recycling. Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean. A reputable waste collector should be employed to remove general refuse on a daily basis. 	Minimize production of the general refuse and avoid odour, pest and litter impacts	Contractor	Work Sites	Construction phase of Advance Works and Main Works of Phase 1A	Waste Disposal (Chemical Waste General) Regulation, Code of Practice on the Packaging, Labelling and Storage of Chemical Waste

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve
	e and Visual		-			-
S7.3.1.1	 Good Site Practices For areas unavoidably disturbed by the Project on a short term basis e.g. works areas, the general principle to try and restore these to their former state to suit future land use, should be adhered to. With regard to topsoil, where identified, it should be stripped, treated appropriately, and where suitable and practical stored for re-use in the construction of the soft landscape works such as roadside amenity strips, and open space sites. 	Minimize the impact to the landscape and visual	Contractor	Work Sites	Prior to construction and construction phase	
\$7.3.2.1	 MM4 - Tree Protection & Preservation Existing trees to be retained within the Project Site should be carefully protected during construction. In particular Old and Valuable Trees (OVTs) will be preserved according to ETWB TC (Works) No. 29/2004. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in Contractor's works areas. A detailed tree survey will be carried out for the Tree Removal Application (TRA) process which will be carried out at the later detailed design stage of the Project. The detailed tree survey will propose which trees should be retained, transplanted or felled and will include details of tree protection measures for those trees to be retained. 	Protect and Preserve Trees	Designer / Contractor	Work Sites	Prior to construction and construction phase	ETWB TCW No. 10/2013, 29/2004 and 3/2006
\$7.3.2.1	 MM5 - Tree Transplantation Trees unavoidably affected by the Project works should be transplanted where practical. Trees should be transplanted straight to their final receptor site and not held in a temporary nursery as far as possible. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, where applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme. A detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBTC 2/2004 and 3/2006 and final 	Transplant Trees where suitable for transplantation	Designer / Contractor	Work Sites where possible. Otherwise consider offsite locations	Prior to construction, construction phase and operation phase	WB TCW No. 10/2013, 3/2006 and 2/2004



EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	When to implement the measures?	What requirements or standards for the measure to achieve			
Landscape	Landscape and Visual								
	locations of transplanted trees should be agreed prior to commencement of the work.								
87.3.2.1	 MM17 - Light Control Construction day and night time lighting should be controlled to minimize glare impact to adjacent VSRs during the Construction phase. Street and night time lighting shall also be controlled to minimize glare impact to adjacent VSRs during the operation phase. 	To minimize glare impact to adjacent VSRs.	Designer / Contractor	Work Sites and/or the Plant	Construction phase and operation phase				
