MTR Corporation Limited

Tsim Sha Tsui Station Northern Subway

Monthly Environmental Monitoring and Audit Report

January 2016

Certified By:

8. ₁

Richard Kwan Environmental Team Leader

Date:

1 2 FEB 2016

MTR Corporation Limited

Tsim Sha Tsui Station Northern Subway

Monthly Environmental Monitoring and Audit Report

January 2016

Verified By:

Sam Tsoi

Independent Environmental Checker

Date:

12 February 2016

EXECUTIVE SUMMARY

The Tsim Sha Tsui Northern Subway Project (TNS) was awarded to the respective contractor in late Dec 2012. The EM&A programme for (TNS) Project commenced on 8 Feb 2013, the commencement date of construction of the Project. This is the thirty-sixth monthly Environmental Monitoring and Audit (EM&A) Report for TNS Project. The Report presents the results of EM&A works for the project works undertaken during the period of January 2016.

The impact monitoring for air quality and noise were conducted for the weeks of January 2016. Both noise and dust monitoring results were below action limits. No environmental notification of summon, prosecution and valid complaint were received in the reporting period.

Regular joint site inspections, led by the ER with the presence with representatives from the Contractor and Environmental Team, were conducted on weekly basis to monitor Contractors' performance on environmental management and implementation of environmental pollution control and mitigation measures for the Project.

The Environmental Permit (EP-317/2009/A), which is a variation to the original permit and issued on 27 January 2014, is being used for the TNS Project.

In the reporting period, no non-conformance was identified and no reporting change of circumstances which may affect the compliance with the recommendations of the EIA Report.

In next reporting period, the key issues are construction of new lift shaft and entrance, and installation of lift and escalators.

EXECUTIVE SUMMARY

- 1 Introduction
 - 1.1 Project Background
 - 1.2 Project Programme
 - 1.3 Coverage of the EM&A Report
- 2 **Project Information**
 - 2.1 Project Management Organization and Contact Details
 - 2.2 Project Works Sites and Areas and Environmental Monitoring Locations
 - 2.3 Summary of EM&A Requirements
 - 2.4 Implementation of Environmental Mitigation Measures
 - 2.5 Construction Activities in the Reporting Month
 - 2.6 Construction Activities in the Coming Month

3 Impact Monitoring

- 3.1 Air Quality
- 3.2 Noise
- 3.3 Action Taken in Event of Exceedance
- 4 Landscape and Visual
 - 4.1 Monitoring Requirements
 - 4.2 Audit Results
 - 4.3 Action Taken in Event of Non-Conformance
- 5 Waste Management
- 6 Water Quality
- 7 Built heritage
- 8 Record of Environmental Complaints
- 9 record of non-Compliances
- 10 Notification of Summons and Successful Prosecutions
- 11 Status of Statutory Submissions
 - 11.1 Submissions required under Environmental Permit
 - 11.2 Statutory Permits and Licenses
- 12 Site Insepctions
 - 12.1 Observations

- 12.2 Other Notable Events
- 13 Future Key Issues
 - 13.1 Key Issues for the Coming Month
 - 13.2 Effectiveness and Efficiency of Mitigation Measures
- 14 Conclusions

List of Appendices

- Appendix A Figures
- Appendix B Environmental Quality Performance Limits
- Appendix C Event Action Plans
- Appendix D Implementation of Environmental Mitigation Measures
- Appendix E Calibration Details
- Appendix F Impact Monitoring Graphical Plots
- Appendix G Monitoring Schedule for the Present and Next Reporting Period

1 INTRODUCTION

1.1 Project Background

MTR Corporation Limited (MTRCL) proposes to construct Tsim Sha Tsui Station Northern Subway, otherwise referred 'TNS'. This EM&A report is for the phase 1 of the TNS, which is the modification of existing Tsim Sha Tsui Station Entrance A1. The scope of this phase 1 work is to upgrade the Entrance A1 to replace the existing concrete structure with a new transparent box reconstructed on the same site with improved access to the station with new disable lift serving Tsim Sha Tsui concourse level, street and Kowloon Park; and escalators serving street and the existing Entrance A1 Adit. The remaining subway running from the north end of Tsim Sha Tsui Station to the new satellite concourse at The One shopping (previous Tung Ying Building) and then to Miramar Shopping Centre will be grouped at the phase 2 of the TNS project. The phase 2 is still under planning stage and the status will be updated later.

1.2 Project Programme

The TNS Project Phase 1 contract with contract number C6564-11C was awarded to the Goldfield N&W Construction Company Limited (GNW) in late Dec 2012. The commencement of construction was on 8 Feb 2013. The commencement of operation of the Project is scheduled to be in 2016. Contractors' tentative programme for the construction is presented below.

| | 2012 | | | | | | 20 | 13 | | | | | | | | | | | 20 | 14 | | | 2013 2014 | | | | | | | | | | | | | | | | | 20 | 16 | | |
|---|------|---|---|---|---|---|----|----|---|---|---|---|---|---|---|---|---|---|----|----|---|---|-----------|---|---|----|---|---|---|---|---|----|---|---|---|---|---|----|---|----|----|---|---|
| Activities | D | J | F | м | Α | м | Т | Т | Α | s | 0 | Ν | D | Т | F | м | Α | м | Т | J | Α | s | 0 | Ν | D | J. | F | м | Α | м | Т | J. | Α | s | 0 | Ν | D | J. | F | м | Α | м | Т |
| Contract Award | ٠ | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Site Clearance | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Construction of Temporary Entrance | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| - Construction Commencement | | | • | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| - Consturction of Temporary Ramp | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| - Installation of Sheet Pile & Pipe Piles and grouting | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| - Construct Temporary Entrance | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| - E&M Installation | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| - ABWF | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Construction of New Entrance | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| - Demolition Existing A1 Entrance | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Installation of Pipe Piles and Grouting | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| - Excavation & Erection Lift Shaft | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| - Construction of New Lift and Entrance | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| - ABWF Works & E&M Works | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Demolition of Temporary Entrance & Reinstatement | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

1.3 Coverage of the EM&A Report

The EM&A programme for the TNS Project commenced on 8 Feb 2013. This is the thirty-sixth Monthly Environmental Monitoring and Audit (EM&A) Report for the Project. The Report presents the results of EM&A works and the impact monitoring for the construction works undertaken by the Contractor during the period of January 2016.

2 PROJECT INFORMATION

2.1 Project Management Organization and Contact Details

The TNS Project organization chart is presented in Figure 1. Contacts of key environmental personnel of the Project are shown in Tables 1a and 1b respectively.

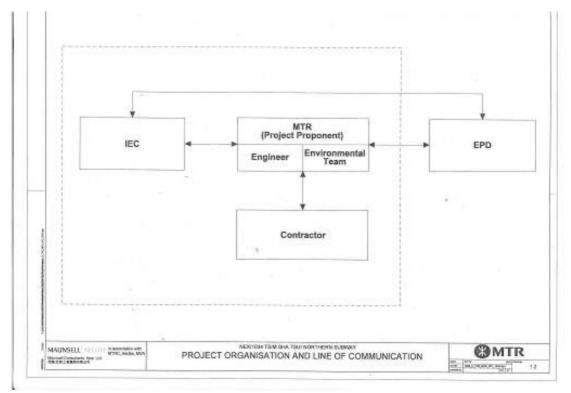


Figure 1 Project Organization

| Organization | Name | Telephone | | |
|-----------------------------------|--------------|-----------|--|--|
| Engineer's Representative | | | | |
| Construction Manager | Kevin Man | 3547 0001 | | |
| Senior Construction Engineer | Jack Chan | 3547 0086 | | |
| Construction Engineer | Andy Chan | 3547 0087 | | |
| Independent Environmental Checker | | | | |
| Arup | Sam Tsoi | 2268 3097 | | |
| Environmental Team | | | | |
| Environmental Team Leader | Richard Kwan | 2688 1179 | | |

 Table 1a
 Contact List of Key Personnel for Project Management

| Table 1b | Contact List of Environmental Authority |
|----------|---|
|----------|---|

| Organization | Name | Telephone |
|--|------------|-----------|
| Environmental Protection Department | | |
| Environmental Protection Officer (Regional East) 61 | Arthur Lee | 2150 8021 |

2.2 Project Works Sites and Areas and Environmental Monitoring Locations

- The TNS Project works sites and areas are summarized in **Table 2** below and shown in **Appendix A** Figure 1.
- The locations of environmental monitoring locations are indicated in Appendix A Figure 2.
- **Table 3** shows the details of the active monitoring stations as reported in Sections 3.1 and 3.2.

| Contact C6564-11C Works Sites and Areas | | | | | | |
|---|--------------------------|--|--|--|--|--|
| Works Sites | Tsim Sha Tsui Entrance A | | | | | |

| ID | Monitoring Station |
|-------|--------------------|
| Air | |
| D1 | Hai Phong Road |
| Noise | |
| M1 | Hai Phong Mansion |
| M2 | Comfort Building |
| M3 | Burlington Arcade |

Table 3Summary of impact air quality and noise monitoring stations

2.3 Summary of EM&A Requirements

The EM&A programme mainly requires environmental monitoring for air quality, noise, landscape & visual, water quality, built heritage and waste management as specified in the EM&A Manual.

A summary of impact EM&A requirements as applicable to this EM&A Report is presented in **Table 4** below.

| Parameters | Descriptions | Locations | Monitoring Frequencies | Duration |
|----------------------------|----------------------------------|-----------------------|---------------------------|-----------------------|
| Air Quality | 24hr- TSP | Shown in Table 3 | Once a week | Construction Stage |
| Noise | Leq(30min) | Shown in Table 3 | Once a week | Construction Stage |
| Landscape and Visual | On-Site Audit | Active Works Sites | Bi-weekly | Construction Stage |
| Built Heritage | On-Site Audit | Active Works Sites | Bi-weekly | Construction Stage |
| Waste | On-Site Audit | Active Works Sites | Weekly | Construction Stage |
| General Site Conditions | Environmental Site Inspection | Active Works Sites | Weekly | Construction Stage |

Table 4Summary of Impact EM&A Requirements

Environmental Quality Performance Limits for air quality and noise are shown in **Appendix B**.

The Event Action Plans for air quality and noise are shown in Appendix C.

2.4 Implementation of Environmental Mitigation Measures

The TNS Civil Works Contractors are required to implement the mitigation measures as specified in the EP, EIA Report and EM&A Manual. During the regular environmental site inspections, the Contractors' implementation of mitigation measures were inspected and reviewed. A schedule of the implementation of mitigation measures identified in the TNS EM&A Manual is given in **Appendix D**.

2.5 Construction Activities in the Reporting Month

Major construction activities carried out by the respective TNS Civil Works Contractors during the reporting period include:

Works Site (Tsim Sha Tsui Entrance A)

- Construction of new lift shaft and entrance
- Installation of lift and escalators

2.6 Construction Activities in the Coming Month

Works Site (Tsim Sha Tsui Entrance A)

- Construction of new lift shaft and entrance
- Installation of lift and escalators

3 IMPACT MONITORING

3.1 Air Quality

24 Hour TSP Level Monitoring

The TSP was measured by Andersen High Volume Sampler, model G25A. The sampling procedure follows that described in the App. B of Pt 50 in 40CFR Ch.1 (U.S. Environmental Protection Agency). TSP is sampled by drawing air through a conditioned, pre-weighed filter paper inside the high volume sampler at a controlled rate. After 24-hour sampling the filter paper with retained particles is collected and returned to the laboratory for drying in a desiccator followed by weighing. TSP levels are calculated from the ratio of the mass of particulate retained on the filter paper to the total volume of air sampled.

The samplers should be properly maintained. Prior to dust monitoring commencing, appropriate checks should be made to ensure that all equipment and necessary power supply are in good working condition.

Calibration Requirements

The flow rate of the high volume sampler with mass flow controller will be calibrated using an orifice calibrator. Initial calibration (five points) will be conducted upon installation and prior to commissioning. Calibration will be carried out every six months. Calibration certificates are attached in **Appendix E**.

To examine the construction dust levels, 24-hour TSP monitoring was undertaken according to the EM&A Manual. The dust monitoring location is shown in the Section 2.2 above. The monitoring location is subjected to construction dust impact from Works Site, is available to check the environmental performance of the work site and assess the effectiveness of the mitigation measures.

Monitoring results are presented in **Table 5** and **Appendix F** for graphical plot. The 24-hour TSP monitoring results in the range from 53.8 to $177.4 \,\mu g/m^3$ recorded in the monitoring period shows that the dust levels generated by the active construction activities were within the Action Levels.

| | | 0 | | | |
|-----------------|--------------------------|--------------------------------------|-------------------------------------|------------------------------|----------------------|
| Date | TSP (µg/m ³) | Action Level (µg/m ³) | Limit Level (µg/m ³) | Compliance to Limit Level | Weather Condition |
| 5 January 2016 | 53.8 | 226 | 260 | Yes | Occasional Rain |
| 12 January 2016 | 59.3 | 226 | 260 | Yes | Sunny |
| 19 January 2016 | 177.4 | 226 | 260 | Yes | Sunny |
| 26 January 2016 | 100.1 | 226 | 260 | Yes | Overcast |

Table 5D1 Hai Phong Road

3.2 Noise

B&K 2250 sound level meters which complied with the International Electrotechnical Commission Publication 651:1979 (Type 1) and 804:1985 (Type 1), specification as referred to in the Technical Memoranda to the NCO were used for the construction noise impact monitoring. The B&K sound level meters and B&K 4231 calibrator are verified by the certified laboratory or manufacturer once every two years to ensure they perform to the same level of accuracy as stated in the manufacturer's specifications. In this reporting period, all relevant calibration certificates are attached in **Appendix E**.

Immediately prior to and following each set of measurements at any NSR, the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. If the calibration levels before and after the measurement differs by more than 1.0dB the measurement shall be repeated to obtain a reliable result. Periods of prolonged or repeated overloading of the sound level meter detector were avoided by setting the meter with adequate headroom prior to commencing measurements. Measurements were recorded to the nearest whole dB, with values of 0.5 or more being rounded up.

Impact noise monitoring of $L_{Aeq(30min)}$ was undertaken to measure construction noise levels in accordance with the EM&A Manual. The noise monitoring locations are shown in Section 2.2 above.

The monitoring results in the range from 65 to 68 dBA are presented in the following **Tables 6a**, **6b** & **6c** and **Appendix F** for graphical plot.

| | | lai i nong i | langion | | | | | |
|-----------------|-------|--|--------------------------|-------------------------|---------------------------------|----------------------|------------------------|--|
| Date | Time | $\begin{array}{c} Measured \\ L_{eq}(dBA) \end{array}$ | Baseline Leq (dBA) | Limit Level (dBA) | Exceedance of Limit Level | Weather Condition | Wind Speed (m/s) | |
| 6 January 2016 | 16:30 | 68 | 71 | 75 | No | Overcast | <2 | |
| 13 January 2016 | 10:30 | 66 | 71 | 75 | No | Sunny | <2 | |
| 20 January 2016 | 14:30 | 67 | 71 | 75 | No | Overcast | <2 | |
| 27 January 2016 | 15:30 | 66 | 71 | 75 | No | Overcast | <2 | |

Table 6aM1 Hai Phong Mansion

* Noise monitoring was carried out during non-raining session.

Table 6bM2 Comfort Building

| Date | Time | $\begin{array}{c} Measured \\ L_{eq}(dBA) \end{array}$ | Baseline Leq (dBA) | Limit Level (dBA) | Exceedance of Limit Level | Weather Condition | Wind Speed (m/s) |
|-----------------|-------|--|--------------------------|-------------------------|---------------------------------|----------------------|------------------------|
| 6 January 2016 | 15:30 | 68 | 70 | 75 | No | Overcast | <2 |
| 13 January 2016 | 10:00 | 67 | 70 | 75 | No | Sunny | <2 |
| 20 January 2016 | 15:00 | 68 | 70 | 75 | No | Overcast | <2 |
| 27 January 2016 | 16:15 | 67 | 70 | 75 | No | Overcast | <2 |

* Noise monitoring was carried out during non-raining session.

Table 6cM3 Burlington Arcade

| Date | Time | Measured L _{eq} (dBA) | Baseline Leq (dBA) | Limit Level (dBA) | Exceedance of Limit Level | Weather Condition | Wind Speed (m/s) |
|-----------------|-------|-----------------------------------|--------------------------|-------------------------|---------------------------------|----------------------|------------------------|
| 6 January 2016 | 16:00 | 66 | 68 | 75 | No | Overcast | <2 |
| 13 January 2016 | 9:30 | 65 | 68 | 75 | No | Sunny | <2 |
| 20 January 2016 | 15:30 | 66 | 68 | 75 | No | Overcast | <2 |
| 27 January 2016 | 16:45 | 66 | 68 | 75 | No | Overcast | <2 |

* Noise monitoring was carried out during non-raining session.

3.3 Action Taken in Event of Exceedance

There was no exceedance in air quality and noise monitoring for the monitoring locations in the reporting period.

4 LANDSCAPE AND VISUAL

4.1 Monitoring Requirements

Monitoring of the implementation of the landscape and visual mitigation measures during construction phase was conducted in accordance with the requirements as stipulated in the EM&A Manual.

The landscape and visual monitoring and audit will be conducted once every two weeks throughout the construction stage.

4.2 Audit Results

Monitoring and audit was undertaken in accordance with the EM&A Manual.

OVT T30 and T31 had fallen due to non-project related causes since the EIA Report, other OVTs were in good health.

The transplantation of the two *Elaeocarpus balansae* in front of Entrance A1 was carried out in May 2013, to sites within Kowloon Park as pre-agreed with LCSD. Both trees have been handed over to LCSD already.

T69, T70 and T71 (all Delonix Regia) at Hai Phong Road were removed on 14 September 2013 as approved under the Tree Removal Applications.

Bi-weekly inspection

The Registered Landscape Architect of Environmental Team or his representatives conducted inspections and audits and the tree protection works were implemented by the respective contractor. No non-conformance was identified in the reporting period.

4.3 Action Taken in Event of Non-Conformance

No actions on landscape and visual were required to be taken in this reporting period.

5 WASTE MANAGEMENT

The quantities disposed in the reporting period are summarized in Table 7:

| Reporting Period | Inert C&D Materials to Public Fill (m ³) | Inert C&D Materials Reused (m ³) | Non-Inert Waste to Landfill (m ³) | Chemical Waste to Designated Treatment Facility (trips) |
|---------------------|--|--|---|--|
| Year 2013 | 715 | 0 | 92 | 0 |
| Year 2014 | 796 | 0 | 8 | 0 |
| Year 2015 | 4,809 | 0 | 6 | 0 |
| Jan 2016 | 18 | 0 | 0 | 0 |
| Total | 6,338 | 0 | 106 | 0 |

| Table 7 | Amount of C | Construction | Waste D | isposed |
|---------|-------------|--------------|---------|---------|
| | mount of C | viisu action | maste D | Isposcu |

6 WATER QUALITY

An effluent discharge license was granted in November 2013. No construction activity would generate major wastewater discharge. Weekly site inspection was conducted to ensure the recommended mitigation measures are properly implemented and license conditions are observed where applicable.

7 BUILT HERITAGE

There are two built heritage resources have been identified in the close proximity to the work site. The two built heritage resources, the retaining wall and the Block S4 of former Whitfield Barracks were inspected visually. They were well kept and no observable impact due to the project was identified. The two granite columns previously relocated to Kowloon Park is in good condition.

8 RECORD OF ENVIRONMENTAL COMPLAINTS

There was no complaint received during the reporting month.

9 RECORD OF NON-COMPLIANCES

There was no non-compliance identified in the reporting period.

10 NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

No summon or prosecution related to environmental issue was recorded in the reporting period. A summary of environmental prosecution since commencement of construction is shown in **Table 8** below:

| Reporting Period | Frequency | Cumulative | Nature | Status |
|------------------|-----------|------------|--------|--------|
| January 2016 | 0 | 0 | N/A | N/A |
| Cumulative | 0 | 0 | N/A | N/A |

Table 8Summary of Prosecution

11 STATUS OF STATUTORY SUBMISSIONS

11.1 Submissions required under Environmental Permit

A summary of the status of the clauses required under the TNS Environmental Permit as of January 2016 is shown in **Table 9** below:

| EP-317/2009 Clause No. | | Description | Status |
|---------------------------|----|--|--|
| 1.11 | 1 | Notification of commencement of construction | Construction commenced on 8 Feb 2013 |
| 2.1 | 2 | Establishment of ET with ET Leader | ET set up since Oct 2012 |
| 2.2 | 4 | Employment of IEC | IEC set up since Oct 2012 |
| 2.3 | 5 | Notification of the management organization of main construction companies and/or any form of JV | Set up in Dec 2012 |
| 2.4 | 6 | Submission of Waste Management Plan | Comments received and RTC is being prepared. The WMP is being revised accordingly |
| 5.4 | 7 | Submission of Baseline Monitoring Report | Submitted |
| 5.7 | 8 | Notification of setting up A community liaison procedure and channel | Established since Jan 2013 |
| 6.2 | 9 | Notification of Internet address to place EM&A data | Established on 7 March 2013 |
| 5.5 | 10 | Monitoring Report for December 2015 | Submitted |

Table 9Summary of EP Submissions

11.2 Statutory Permits and Licenses

A summary of the status of all relevant environmental permits and licenses as of 31 January 2016 is shown in **Table 10** below:

| Descriptions | License / Permit Reference | Issue Date | Expired Date |
|--|----------------------------|-----------------|--------------|
| Environmental Permit for Tsim Sha Tsui Station Northern Subway Project | EP-317/2009/A | 27 January 2014 | NA |
| Wastewater Discharge License | WT00017459-2013 | 1 November 2013 | 30 Jun 2018 |

Table 10Summary of Permits and Licenses

| Descriptions | License / Permit Reference | Issue Date | Expired Date |
|--|--|---------------|--------------|
| Registration as a Chemical Waste Producer | Waste Producer Number: 5213-214-G2417-05 | 12 March 2013 | NA |
| Disposal of Construction Waste | Billing Account no. 7016610 activated | 27 Dec 2012 | NA |
| Construction Noise Permit | GW-RE1329-15 | 29 Dec 2015 | 15 Jan 2016 |

A variation to the Environmental Permit has been granted by EPD on 27 January 2014. The variation concerns works near OVT 73 and demolition existing exit.

12 SITE INSEPCTIONS

12.1 Observations

Regular site inspections led by the Engineer's Representative and anticipated by ET and respective Contractors were undertaken in accordance with the EM&A Manual in the reporting period. The contractors' performance on environmental matters were assessed and found in an acceptable manner. The inspection findings and the associated recommendations on improvement to the environmental protection and pollution control works were raised to the contractors for reference and/ or action.

Observations against the implementation of the mitigation measures recommended in the EP/EIA are summarized in **Table 11** as follows:

| Item | Description | Follow-up Status |
|------|--|---------------------|
| | Contract C6564-11C | |
| 1 | The contractor was reminded that the noise and dust mitigation requirements stated in the EP shall be strictly followed. | On-going |
| 2 | The contractor was reminded to pay special attention to the Heritage Built and the OVT protection. | On-going |

Table 11Observations

The respective contractors have followed most of concerned items raised during the inspections for rectification in a responsible manner.

12.2 Other Notable Events

IEC Site Inspection

The IEC conducted site inspections for Works Areas on 5 January 2016. Some observations listed in section 12.1 were noted during the site inspections and the respective Contractors had followed up the issues as identified in the site inspections in a responsible manner.

EPD Inspection

EPD inspection was conducted on 27 January 2016.

13 FUTURE KEY ISSUES

13.1 Key Issues for the Coming Month

Future key issues envisaged in the coming month include the followings:

- Construction of new lift shaft and entrance
- Installation of lift and escalators

13.2 Effectiveness and Efficiency of Mitigation Measures

Based on the environmental monitoring results of the reporting period, the effectiveness and efficiency of the mitigation measures implemented were found to be satisfactory. The respective contractors were reminded to carry out their future construction activities to comply with the requirements of the EP and the relevant contract requirements.

14 CONCLUSIONS

The Report presents the results of EM&A works and the impact monitoring for the construction works undertaken during January 2016. The major construction activities in the reporting period were:

- Construction of new lift shaft and entrance
- Installation of lift and escalators


No exceedance on noise and dust action level and no complaint received.

No notification of summon and prosecution were received in the reporting period.

Regular site inspections led by the Engineer's Representative and participated by the representatives from ET and the respective Contractors' Team were conducted on a weekly basis to monitor the implementation of environmental pollution control and mitigation measures for the Project. No non-conformance to the environmental requirements was identified by the Environmental Team in the reporting period. The performances of the respective contractors on site environmental management were found in a responsible manner in this reporting period.

It is concluded from the environmental monitoring and audit works for the Tsim Sha Tsui Northern Subway Project were undertaken in a responsible manner. The environmental protection and pollution control measures provided by the contractor were generally acceptable. <u>Appendix A</u> <u>Figures</u>

Figure 1. TNS Project Works Area

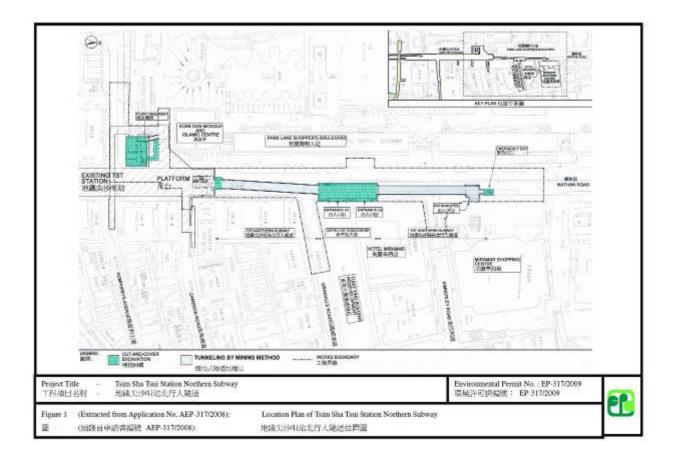

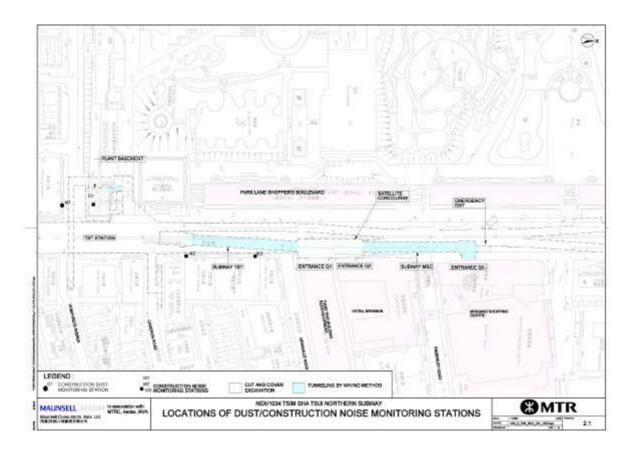


Figure 2. TNS Project Dust and Noise Monitoring Location Plan

<u>Appendix B</u> <u>Environmental Quality Performance Limits</u>

Action and Limit Level for 24-hour TSP

| Monitoring Station | Action Level (µg/m ³) | Limit Level (µg/m ³) |
|--------------------|-----------------------------------|----------------------------------|
| D1 | 226 | 260 |

Action and Limit Level for 1-hour TSP for Complaint Handling

| Monitoring Station | Action Level (µg/m ³) | Limit Level (µg/m ³) |
|--------------------|-----------------------------------|----------------------------------|
| D1 | 310 | 500 |

Action and Limit Level for Construction Noise

| Time Period | Action Level | Limit Level (dB(A)), |
|-----------------------|-----------------------|----------------------|
| | | Leq(30min) |
| 0700-1900 hr on norma | When one documented | 75 |
| weekdays | complaint is received | |

<u>Appendix C</u> <u>Event Action Plans</u>

MAUNSELL AECOM

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

Table 2.3 Event / Action Plan for Air Quality (Dust)

| Fvent | | Action | 「「「「「」」」」」」」」」」」」」」」」」」」」」」」」」」」」」」」 | ののたちに見るないので、 | 10 |
|-----------------------------------|---|---|---|---|----|
| WIDAY | and the second se | Contractor | 8 | IEC | |
| Action Level being exceeded | Action Level 1. Conduct additional being measurement to confirm finding. 2. Identify source and investigate the causes of exceedance, if caused by MTRCL's work. | Discuss with ET on proper remedial actions. Submit proposals for remedial actions to ER within 3 working days of notification. | Confirm receipt of notification of exceedance. Notify Contractor. Check Contractor's working methods. | Check Contractor's working method. Advise ET on the effectiveness of the proposed remedial measures. | |
| | Inform IEC, ER and Contractor. Discuss with IEC, ER and Contractor on remedial actions required. | Amend proposal If appropriate. Implement the agreed proposals. | Agree with the Contractor on the remedial measures to be implemented. Ensure proper | | |
| | If necessary, conduct additional monitoring to assess the effectiveness of Contractor's remedial actions. | Liaise with ER to optimize the effectiveness of the agreed mitigation. | implementation of remedial measures. 6. Assess the efficiency of remedial actions and hour | | |
| | If exceedance continues, arrange meeting with IEC and ER to review implementation and identify further appropriate mitration measures | | the Contractor informed. | | |
| | 7. If exceedance stops, cease additional monitoring. | Đ. | | | |

1

MAUNSELL ALCOM

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

ļ

| Event | | Action | | and the set of the set |
|-------------------|---|--|---|--|
| | 6 | Contractor | , B | IEC |
| being exceeded | Conduct additional measurement to confirm findings. Identify source and investigate the causes of exceedance; Notify EPD, IEC, ER and Contractor. Check Contractor's working procedures. Check Contractor's working procedures. Discuss with IEC, ER and Contractor on remedial actions required. If necessary, conduct additional monitoring to assess effectiveness of Contractor's remedial actions. Keep EPD, IEC and ER informed of the monitoring results. If exceedance continues, arrange meeting with IEC and ER to review implementation and identify further appropriate mitigation measures. If exceedance stops, cease additional monitoring. | Take immediate action to avoid further exceedance. Discuss with ET and ER on proper remedial actions. Submit proposals for remedial actions to ER within 3 working days of notification. Implement the agreed proposals. Liaise with ER to optimize agreed mitigation. | Confirm receipt of notification of exceedance. Notify Contractor. Check Contractor's working methods. Agree with the Contractor on the remedial measures to be implemented. Ensure proper implementation of remedial measures. Assess the efficiency of remedial actions and keep the Contractor informed. | Check Contractor's working method. Feview Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ET accordingly. |

September 2008

2-7

MAUNSELL AECOM

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

Table 3.3 Event and Action Plan for Construction Noise

| Contraction of the other | いいの 日本 一日 | Action | on several data and the several data and | |
|--------------------------------------|---|---|--|---|
| Event | 1 | Contractor | ER | EC |
| Action Level being exceeded | Undertake measurement to establish validity of complaint. Identify source(s) of complaint. Notify IEC, ER and Contractor. Discuss with the IEC, ER and Contractor on remedial measures required. Increase monitoring frequency to check mitigation effectiveness. If excceedance continues, arrange meeting with IEC and ER to review implementation and identify further appropriate mitigation measures. If excceedance stops, cease additional monitoring. | Submit noise mitigation proposals to ER within three working days of notification. Amend proposal if appropriate. Implement noise mitigation proposals. Liaise with ER to optimize the effectiveness of the agreed mitigation. | Confirm receipt of notification of complaint. Notity Contractor. Notity Contractor. Check Contractor's working methods. Agree with the Contractor on the remedial measures to be implemented. Ensure proper implementation of remedial measures. Assess the efficiency of remedial actions and keep the Contractor informed. Inform complainant of actions taken. | Check Contractor's working methods. Review the proposed remedial measures by the Contractor and advise the ET accordingly. |

September 2008

3-4

MAUNSELL APCOM

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

| Fvent | 22 | 「「「「「「「」」」」」」」」」」」」」」」」」」」」」」」」」」」」」」 | Action | n New State State Party | Burger Real | のないというないないである | No. State |
|-------------------------------------|----|--|---|---|--|---|---------------|
| | 1 | E | Contractor | ER | - Contraction | IEC | |
| Limit Level being exceeded | | Repeat measurement to confirm findings. Identify source and investigate the cause of exceedance. Inform EPD, IEC, ER and Contractor. Contractor. Contractor. Discuss with the IEC, Contractor and ER on remedial measures required. Discuss with the IEC, Contractor and ER on remedial measures required. Increase monitoring frequency to assess effectiveness of Contractor's mitigation actions and keep EPD, IEC and ER informed the results. If exccedance continues, arrange meeting with IEC and ER to review implementation and identify further appropriate mitigation measures. | Take immediate action to avoid further exceedance. Submit proposals for exceedance. Submit proposals for remedial actions to ER within 3 working days of notification. Implement the agreed proposals. Liaise with ER to optimize the effectiveness of the agreed mitigation. | Confirm receipt of notification of exceedance. Notify Contractor. Check Contractor's working methods. Agree with the Contractor on the remedial measures to be implemented. Ensure proper implementation of remedial measures. Assess the efficiency of remedial actions and keep the Contractor informed. | of c's working ontractor neasures d. f remedial and keep ormed. | Check Contractor's working methods. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ET accordingly. | / to eness |
| | ΰ | It exceedance stops, cease additional monitoring. | | | | | |

September 2008

.

X.

3-5

<u>Appendix D</u> <u>Implementation of Environmental Mitigation Measures</u>

MAUNSELL AFCOM

IMPLEMENTATION SCHEDULE OF THE PROPOSED MITIGATION MEASURES APPENDIX B

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Implementation Agent | Location of the Measure | When to implement | Relevant Legislation and Guidelines |
|------------|--------------|---|---------------------------------------|----------------------------|-----------------------|---|
| Constructi | on Air Que | Construction Air Quality Impact | No. Sol and a long of the long of the | 「日本になるのないの」 | | たいというのでのない |
| 3.10.1 | 2.9.2 | watering of active construction works area twice a day skip hoist for material transport shall be totally enclosed by impervious sheeting | Contractor | Works Area | Construction Phase | EIAO-TM Air Pollution Control |
| | | every vehicle shall be washed to remove any dusty materials from its body and wheels before leaving a construction site | | | | (Construction Dust) Regulation |
| | | the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point shall be paved with concrete, bituminous materials or hardcores | | | | |
| | | where a site boundary adjoins a road, streets or other accessible to the public, hoarding of not less than 2.4m high from ground level shall be provided along the entire length except for a site entrance or exit | | | | |
| | | every stack of more than 20 bags of cement shall be covered entirely by impervious sheeting places in an area sheltered on the top and the 3 sides | 4 | | • | |
| | | all dusty materials shall be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet | | | | |
| | | the height from which excavated materials are dropped shall be controlled to a minimum practical height to limit fugitive dust generation from unloading | 0.233 | | | |
| | | stockpile of excavated or dusty materials shall be covered entirely by clean impervious sheeting | 11201 | | | |
| | | the load of dusty materials carried by vehicle leaving a construction site shall be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle | | | | |
| | | instigation of an environmental monitoring and auditing | | | | |

September 2008

App B.1/1

MAUNSELL AECOM

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Implementation Agent | Location of the Measure | When to implement | Relevant Legislation and Guidelines |
|---------------------------|--------------|---|-------------------------|------------------------------|-----------------------|---|
| | | program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise | | | | |
| Construction Noise Impact | ion Noise | Impact | | States - States and a second | 「「ないないのないのない」 | 「「「「「「「」」」」」」 |
| 4.9.2- 4.9.3 | 3.8.1 | Adoption of Quieter PME | Contractor | Works Area | Construction Phase | EIAO-TM Noise Control Ordinance |
| 4.9.4 | 3.8.1 | Use of Movable Noise Barrier 5 dB(A) reduction for movable PME and 10 dB(A) for stationary PME can be achieved depending on the actual design of movable noise barrier Barrier material of surface mass in excess of 7 kg/m² is recommended to achieve the predicted screening effect | Contractor | Works Area | Construction Phase | EIAO-TM Noise Control Ordinance |
| 4.9.5 | 3.8.1 | Use of Noise Enclosure/Acoustic Shed Noise Enclosure or Acoustic Shed is to cover stationary PME such as air compressor and concrete pump. With the adoption of the noise enclosure, the PME could be completely screened, and noise reduction of 15 dB(A) can be achieved according to the GW-TM | Contractor | Works Area | Construction Phase | EIAO-TM Noise Control Ordinance |
| 4.9.6 | 3.8.1 | Use of Silencer Silencers are recommended to be used in fan ventilation Silencers are recommended to be used in fan ventilation system to attenuate noise generated during fan operation to achieve a noise reduction of 15dB(A). The Contractor shall be responsible for selection of appropriate silencers for the ventilation fans. | Contractor | Works Area | Construction Phase | EIAO-TM Noise Control Ordinance |
| 4.9.7 | 3.8.1 | Use of Noise Insulating Fabric Noise insulating fabric (the Fabric) can be adopted for certain PME (e.g. drill rig, pilling auger etc) The Fabric should be lapped such that no opening or gaps on the joints. Technical data from manufacturer states that by using the Fabric, a noise reduction of over 10 dB(A) can be achieved on noise level (Reference was | Contractor | Works Area | Construction Phase | EIAO-TM Noise Control Ordinance |

September 2008

App B.1/2

MAUNSELL APCOM

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

| EIA Ref. | EM&A Ref. | 201010.001255 | Hecommended Mitigation Measures | Implementation Agent | Location of the Measure | When to Implement | Relevant Legislation | and |
|-------------------------------|--------------|---------------|---|--|---|-----------------------|---------------------------------------|-----|
| | | | made from Modifications to MTRC Tsim Sha Tsui Station Variation of Environmental Permit EP-113/2001/C). As an conservative approach, a noise reduction of 10 dB(A) for the PME lapped with the Fabric was assumed. | | | | COLIDORAD | |
| 4.6.6 | 3.8.1 | | Decking over the excavation areas at the Entrance A1 and satellite concourse | Contractor | Works Area | Construction Phase | EIAO-TM Noise Control Ordinance | |
| 4.10.8 | 3.8.1 | <u>Good</u> | Good Site Practices | Contractor | Works Area | Construction Phase | EIAO-TM Noise Control | |
| | | • | Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program. | ł | | | Ordinance | |
| | | • | Silencers or mufflers on construction equipment shall be utilised and shall be properly maintained during the construction program. | | | | | |
| | | • | Mobile plant, if any, shall be sited as far away from NSRs as possible. | | | | | |
| | | • | Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum. | | | • | | |
| | | • | Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. | | | | | |
| | | | Material stockpiles and other structures shall be effectively utilised, wherever practicable, in screening noise from on-site construction activities. | | | | | |
| Operation Noise Impact | Noise Imp | pact | | Section of the sectio | A CONTRACTOR OF | 「二十二」の | Contraction of the second | 1 |
| Table 4.8 | Table 3.4 | | The maximum Sound Power Levels (SWLs) for the ventilation shaft openings shall be complied with during the selection of ventilation fans and mitigation measures. | Designer | Station, ventilation shafts and E&M plant items | Design Phase | EIAO-TM | |

September 2008

App B.1/3

MAUNSELL AECOM

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

| EIA Ref. | EM&A Ref. | Reco | Implementation Agent | Location of the Measure | When to implement | Relevant Legislation and |
|-------------|--------------|--|-------------------------|---|----------------------------------|---|
| 9. 0 | N 5 10 | Choose quieter plant such as those which have been effectively silenced. Include noise levels specification when ordering new plant (including chillier and E/M equipment). Locate fixed plant/louver away from any NSRs as far as practicable. Locate fixed plant in walled plant rooms or in specially designed enclosures. Locate building. Locate noisy machines in a basement or a completely separate building. Install direct noise mitigation measures including silencers, acoustic louvers and acoustic enclosure where necessary. Develop and implement a regularly scheduled plant maintenance programme so that equipment is properly operated and serviced in order to maintain controlled level of noise. The programme should be implemented by properly trained personnel. | Contractor | Station, ventilation shafts and E&M plant items | Design / Operational Phase | EIAO-TM Noise Control Ordinance |
| Constructic | in Water (| Construction Water Quality Impact | 小学校の一学会社が大学 | 「日本の」 「日本のような」」な | | All sold holds and sold all sold sold and sold all sold a |
| 5.13.2 | 4.3.2 | Construction runoff and site drainage should be prevented or minimized in accordance with the guidelines stipulated in ProPECC PN 1/94 "Construction Site Drainage". The specified mitigation measures and practices include the following: Provision of perimeter drains to intercept off-site water around the site with internal drainage works and erosion and sedimentation control facilities implemented. These shall be constructed in advance of site formation works and earthworks. Earth bunds or sand bag barriers shall be provided on-site to direct storm water to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the Contractor prior to the commencement of construction. | Contractor | Works Area | Construction Phase | ProPECC PN 1/94 Construction Site Drainage EIAO-TM Water Pollution Control Ordinance Waste Disposal Ordinance |

September 2008

App B.1/4

| and | | | | | | | |
|--|---|--|---|---|---|--|--|
| Relevant Legislation Guidelines | | 2 | | | | | |
| When to implement | | | | | • | | |
| Location of the Measure | | | | | | | |
| Implementation Agent | | | | | | | |
| EM&A Recommended Mitigation Measures Ref. | structures shall be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly during rainstorms. Deposited slit and grit shall be regularly removed, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times. | Exposed slope/soil surface shall be covered by tarpaulin as soon as possible to reduce the potential of soil erosion. Arrangements should always be in place to ensure that adequate surface protection measures can | be safely carried out well before the arrival of a rainstorm. Other measures that need to be implemented before, during and after rainstorms are summarized in ProPECC PN 1/94. | Open stockpiles of construction materials (e.g. aggregates, sand and fill material) or construction wastes on-site shall be covered with tarpaulin or similar fabric during rainstorms. | Construction works shall be programmed to minimise surface excavation works during the rainy seasons (April to September). All exposed earth areas shall be completed and vegetated as soon as possible after | earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where | during the rainy season, or all carinot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed surfaces shall be covered by temorils or other means |
| EM&A Ref. | | | | | | | |
| EIA Ref. | | | | | | | |

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

Manholes shall always be adequately covered and temporarily sealed so as to prevent silt, construction

by tarpaulin or other means.

.

materials or debris being washed into the drainage system and storm runoff being directed into foul sewers. rainstorms are likely, actions to be taken when a · · Precautions be taken at any time of year when

September 2008

App B.1/5

Rev. A

MAUNSELL AECOM

| EIA Ref. | EM&A Ref. | Recomm | Recommended Mitigation Measures | Implementation Agent | Location of the Measure | When to implement | Relevant Legislation and |
|------------------|------------------|--|---|-------------------------|----------------------------|----------------------|--|
| | | All we have a constraints All we have a constraints All we have a constraints Constraints Constraints Constraints | rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequate designed and sited wheel washing facilities shall be provided at every construction site exit, where provided at every construction site exit, where the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road shall be paved with sufficient tracking of soil and sitty water to public roads and drains. Oil interceptors shall be provided in the drainage system downstream of any oil/fuel pollution sources. The oil interceptors shall be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass shall be provided for the oil interceptors to prevent flushing during heaving rain. Construction sold waste, debris and rubbish on site shall be collected, handled and disposed of property to avoid water quality impacts. | | | | Guidelines |
| 5.13.6 5.13.6 | 4.3.3 - 4.3.5 | Underground Work Underground Imit the amo exposed are September). Uncontaminat tanks prior to The wastewat | rground Work Underground works shall be conducted sequentially to limit the amount of construction runoff generated from exposed areas during the wet season (April to September). Uncontaminated discharge shall pass through settlement tanks prior to off-site discharge. | Contractor | Works Area | Phase | ProPECC PN 1/94 Construction Site Drainage EIAO-TM Water Pollution Control Ordinance |

Rev. A

September 2008

App B.1/6

MAUNSELL AFCOM

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Implementation Agent | Location of the Measure | When to implement | Relevant Legistation and Guidelines |
|----------|------------------|--|---|----------------------------|-----------------------|--|
| | | water in underground area with a high concentration of SS shall be treated (e.g. by settlement in tanks with sufficient retention time) before discharge. Oil interceptors would also be installed to remove the oil, lubricants and grease from the wastewater. | | | | |
| 5.13.7 | 4.3.6 | Sewage Effluent Temporary sanitary facilities, such as portable chemical toilets, shall be employed on-site where necessary to handle sewage from the workforce. A licensed contractor would be responsible for appropriate disposal of waste matter and maintenance of these facilities. | Contractor | Works Area | Construction Phase | ProPECC PN 1/94 Construction Site Drainage EIAO-TM Water Pollution Control Ordinance |
| 5.14.2 - | 4.3.8 | General Construction Site Activities Debris and rubbish generated on-site shall be collected, handled and disposed of properly to avoid being flushed or blown by wind into the drainage culvert. Stockpiles of cement and other construction materials should be kept covered when not being used. Oils and fuels shall only be used and stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents, all fuel tanks and storage areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund shall be drained of rainwater after a rain event. | | | * | |
| Waste Ma | Waste Management | 10.00 | 一日 二日 | のためになるのである | のないないないである | のないのないのないです。 |
| 6.7.1 | 5.2.3 | Good Site Practices Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site. | Contractor | Works Area | Construction Phase | EIAO-TM Waste Disposal Ordinance ETWB TCW No. 19/2005 |

Rev. A

*

September 2008

App B.1/7

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Implementation Agent | Location of the Measure | When to implement | Relevant Legislation Guidelines | and |
|----------|--------------|--|-------------------------|----------------------------|----------------------|---------------------------------------|-----|
| | | Training of site personnel in proper waste management and chemical waste handling procedures. Provision of sufficient waste disposal points and regular collection for disposal. | | | | | |
| | | Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers. | | | | | |
| | | Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. | | | | | |
| | | A Waste Management Plan should be prepared and submitted to the Engineer for approval. One may make reference to ETWB TCW No. 19/2005 for details. | | | | | |
| | | A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be proposed. | | | | | |
| 6.7.2 | 5.2.4 | In order to monitor the disposal of C&D materials at public fill reception facilities, as appropriate, and to control fly tipping, a trip-ticket system should be included as one of the contractual | | | - | | |
| 010 | | requirements. | | | | | |
| 6.7.3 | 5.2.5 | Waste Reduction Measures | Contractor | Works Area | Construction | EIAO-TM | |
| | | Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal. | | | Phase | | |
| | | Encourage collection of aluminium cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force. | | × | | | |
| | | Any unused chemicals or those with remaining functional capacity shall be recycled. | | | | | |
| | | Proper storage and site practices to minimise the potential for damage or contamination of construction materials. | | | × | | |

NEX/1034 Tsim Sha Tsui Station Northern Subway

Rev. A

September 2008

App B.1/8

-

MAUNSELL AECOM

MAUNSELL AECOM

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

| EIA Hef. | EM&A Ref. | Recommended Mitigation Measures | Implementation Agent | Location of the Measure | When to implement | Relevant Legislation and Guidelines |
|------------------|------------------|--|-------------------------|----------------------------|-----------------------|---|
| | | Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. | | | | |
| 6.7.6 & 6.7.7 | 5.2.7 - 5.2.8 | | Contractor | Works Area | Construction Phase | ETWB TCW No. 33/2002 |
| | | Within stockpile areas, the following measures shall be taken to control potential environmental impacts or nuisance: | | | | ETWB TCW No. 19/2005 |
| | | covering stockpile of C&D material entirely by clean impervious sheet to reduce potential dust impact. | 1 | | 1 | |
| | | locating stockpiles to minimise potential visual impacts. minimizing land intake of stockpile areas as far as possible. | | | | |
| | - | When disposing C&D material at a public fill reception facility, the material shall only consist of soil, rock, concrete, brick, cement plaster/mortar, inert building debris, aggregates and asphalt. | 1 | | | |
| | | The material shall be free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered to be unsuitable by the Filling Supervisor. | | | | |
| 6.7.8 | 5.2.9 | Chemical Wastes | Contractor | Works Area | Construction | EIAO-TM |
| | 114 | After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. | | | Dobill | Waste Disposal (Chemical Waste) (General) Regulation |
| | | Spent chemicals should be collected by a licensed collector for disposal at the CWTC or other licensed facility. | | 2 | | |
| 6.7.9 | 5.2.10 | General Refuse General refuse shall be stored in enclosed bins or compaction units separate from C&D material. | Contractor | Works Area | Construction Phase | Public Health and Municipal Services Ordinance |

September 2008

App B.1/9

Rev. A

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Implementation Agent | Location of | When to | 1 123/60 |
|-----------------------------|--------------|--|--------------------------------------|----------------------------------|-----------------------|-----------------------------------|
| | | contractor to remove general refuse from the site, separately from C&D material. | | | lieuadu | Legislation and Guidelines |
| | | Preferably an enclosed and covered area shall be provided to reduce the occurrence of 'wind blown' light material. | | | | |
| Landscape and Visual Impact | e and Visu | al Impact | Conditional Condition (Construction) | | | |
| Table 7.5 | 6.3.1 | CM1: Existing trees including OVTs to be retained and maintained on site should be carefully protected during construction. Encroachment of any works close to the drip line of OVTs should be avoided. CM2: Trees of high amenity and survival rate after transplanting which unavoidably affected by the works should be transplanted where practical. CM3: Control-of night – time lighting. CM4: Erection of decorative screen hoarding compatible with surrounding coding. | Contractor | Works Area | Construction Phase | EIAO-TM |
| Table 7.6 | 6.3.1 | OM1: Aesthetic design of Entrance A1 Minimization | | | 4 | |
| | | | Contractor | Works Area | Operation Phase | EIAO-TM |
| Built Heritage Impact | ge Impact | | The second statement of the second | Contraction of the second second | | |
| | 7.1.1 | Temporary removal of the two granite columns (east of brick wall of modern extension of Block S4) and will be stored securely during construction period, and reinstated back to its original location after completion of works. | Contractor | Works Area | Construction | EIAO-TM |
| 8.8.1 - | 7.2.4 | Precautions shall be taken throughout the construction stage to prevent any damage to the historical building. Structural monitoring system, including preconstruction survey shall be designed and implemented by a Registered Structural Engineer to ensure compliance with the Building Ordinance. Consult AMO on any other mitigation measures that | Contractor | Works Area | Construction Phase | EIAO-TM; Building Ordinance |

ċ NEX/1034 Tsim Sha Tsui Station North

MAUNSELL AECOM

Rev. A

App B.1/10

Contraction Contraction

MAUNSELL AFCOM

NEX/1034 Tsim Sha Tsui Station Northern Subway EM&A Manual

| Ref. | EM&A Ref. | EIA Ref. EM&A Recommended Mitigation Measures Ref. | Implementation Agent | Location of When to Relevant the Measure implement Legislatio | When to implement | 5 4 | and |
|------|--------------|---|-------------------------|--|----------------------|-----|-----|
| | | would be required administratively or under Antiquities and Monuments Ordinance. Implement these requirements from AMO during the construction period. use of sensibly designed hoardings to minimize the temporary visual impact during construction phase | | | | | |

September 2008

App B.1/11

d

Rev. A

2

<u>Appendix E</u> <u>Calibration Details</u>

ANDERSEN INSTRUMENTS INC.

GS2310 Series Sampler Calibration

| | D' 1 | D I V | 1 |
|---|---------|-----------|---|
| (| LICKSOF | Recorder) |) |
| | | | |

| Custor | ner -> MTRC | (Die | SITE | Certificate -> | 20150901 | |
|-------------------|-----------------------|-----------------------|---------|----------------|-------------------|----------|
| Locat | ion -> TNS | | | Date -> | 4-Sep-15 | |
| Samp | oler -> 1294-10 | 96 | | | Chan Kin Fung | |
| | | C | ONDITIO | | | |
| Sea Level Pressur | e (hpa) | 1013.1 | | Sampler Eleva | ation (feet) | 50 |
| Sea Level Pressur | e (in Hg) | 29.92 | | Corrected Pres | ssure (mm Hg) | 758.56 |
| Temperature | (deg C) | 29.1 | | Temperature | (deg K) | 302.10 |
| Seasonal SL Press | sure (in Hg) | 29.92 | | Corrected Sea | sonal (mm Hg) | 758.56 |
| Seasonal Tempera | ature (deg C) | 29.10 | | Seasonal Tem | perature(deg K) | 302.10 |
| | | CALIBI | RATION | ORIFICE | | |
| Make - | > TISCH | | | | Qstd Slope -> | 2.02007 |
| Model | -> TE-502 | 5A | | | Qstd Intercept -> | -0.0218 |
| Serial# | -> 157N | | | | Date Certified -> | 6-Aug-15 |
| | | CA | LIBRAT | ION | | |
| Plate | e or H ₂ O | Qstd | Ι | IC | LINEAR | |
| Tes | t # (in) | (M ³ /min) | (chart) | (corrected) | REGRESSION | |
| 1 18 | 3 12.3 | 1.733 | 59 | 58.543 | Slope = | 30.1694 |
| 2 13 | 9.6 | 1.533 | 53 | 52.589 | Intercept = | 6.4126 |
| 3 10 | 7.5 | 1.356 | 48 | 47.628 | Corr. Coeff. = | 0.9998 |
| 4 7 | 4.9 | 1.098 | 40 | 39.690 | | |
| 5 5 | 2.9 | 0.847 | 32 | 31.752 | | |
| Calcula | tions | | | | | |

Calculations

 $Qstd = 1/m [Sqrt (H_2O (Pa/Pstd) (Tstd/Ta)) - b]$ IC = I [Sqrt (Pa/Pstd) (Tstd/Ta)]

Qstd = standard flow rate IC = corrected chart response I = actual chart response m = calibrator Qstd slope b = calibrator Qstd intercept Ta = actual temperature during calibration (deg K) Pa = actual pressure during calibration (mm Hg) Tstd = 298 deg KPstd = 760 mm HgFor subsequent calculation of sampler flow: 1/m ((I) [Sqrt (298/Tav) (Pav/760)] - b)

m = sampler slope b = sampler intercept I = chart response Tav = daily average temperature Pav = daily average pressure

This is to certify that the above equipment has been calibrated in accordance with manufacturer's procedure.



線合 試 験 有 限 公司 SOILS & MATERIALS ENGINEERING CO., LTD. G/F. 9/F., 12/F., 13/F. & 20/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong, 育徳黄竹坑道3 7 號列達中心地下、9 樓, 1 2 樓, 1 3 樓及20 樓 E-mail: smec@cigismec.com Website: www.cigismec.com





CERTIFICATE OF CALIBRATION

| Certificate No.: | 14CA1120 03-01 | | | Page | 1 | of | 2 |
|---------------------------------|---|--------------------|---------|-----------------------|-------|-----------|--------------------|
| Item tested | | | | | | | |
| Description: | Sound Level Meter | (Type 1) | | Microphone | | | |
| Manufacturer: | B&K | | | B&K | | | |
| Type/Model No.: | 2250 | | | 4189 | | | |
| Serial/Equipment No .: | 2749852 | | | 2695393 | | | |
| Adaptors used: | | | | • | | | |
| Item submitted by | | | | | | | |
| Customer Name: | MTR Corporation L | imited | | | | | |
| Address of Customer: | - | | | | | | |
| Request No.: | | | | | | | |
| Date of receipt: | 20-Nov-2014 | | | | | | |
| | | | | | | | |
| Date of test: | 21-Nov-2014 | | | | | | |
| Reference equipment | used in the calibr | ation | | | | | |
| Description: | Model: | Serial No. | | Expiry Date: | | Traceal | ble to: |
| Multi function sound calibrator | B&K 4226 | 2288444 | | 20-Jun-2015 | | CIGISM | EC . |
| Signal generator | DS 360 | 33873 | | 09-Apr-2015 | | CEPREI | |
| Signal generator | DS 360 | 61227 | | 09-Apr-2015 | | CEPREI | |
| Ambient conditions | | | | | | | |
| Temperature: | 21 ± 1 °C | | | | | | |
| Relative humidity: | 60 ± 10 % | | | | | | |
| Air pressure: | 1010 ± 10 hPa | | | | | | |
| | | | | | | | |
| Test specifications | | | | | | | |
| | ter has been calibrate | | ith the | requirements as spe | cifie | d in BS 7 | 580: Part 1: 199 |
| | in procedure SMTP00 vere performed using a | | substi | tuted for the microph | one | which wa | is removed and |
| | alent capacitance with | | | tatoa ioi alo moropii | | | |
| | ion was performed us | | | | ions | was app | lied for the diffe |
| between the free-field | d and pressure respor | isess of the Sound | Level | Meter. | | | |
| | | | | | | | |
| Test results | | | | | | | |

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Approved Signatory:

Huang Jian Min/Fjeng Jun Qi

Date: 22-Nov-2014 Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-1/Issue 1/Rev.C/01/02/2007

Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. 028 - CAL) under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific calibration activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation. Such terms of accreditation stipulate that the results shall be traceable to the International System of Units (S.I.) or recognised measurement standards. This certificate shall not be reproduced except in full.



綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 6/F. 9/F. 12/F. 13/F. & 20/F. Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. 香港黄竹坑道37號利達中心地下,9樓,12樓,13樓及20樓 E-mail: smec@cigismec.com Website: www.cigismec.com

Tel : (852) 2873 6860 Fax : (852) 2555 7533



(Continuation Page)

2 2 Certificate No.: 14CA1120 03-01 Page of

CERTIFICATE OF CALIBRATION

1, Electrical Tests

> The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

| Trat | Subtest: | Status: | Expanded Uncertanity (dB) | Coverage Factor |
|-------------------------|--|---------|------------------------------|--------------------|
| Test: | Sublest. | otatus. | Gildertainty (ub) | 1 40101 |
| Self-generated noise | A | Pass | 0.3 | |
| - | С | Pass | 0.8 | 2.1 |
| | Lin | Pass | 1.6 | 2.2 |
| Linearity range for Leq | At reference range , Step 5 dB at 4 kHz | Pass | 0.3 | |
| , . | Reference SPL on all other ranges | Pass | 0.3 | |
| | 2 dB below upper limit of each range | Pass | 0.3 | |
| | 2 dB above lower limit of each range | Pass | 0.3 | |
| Linearity range for SPL | At reference range , Step 5 dB at 4 kHz | Pass | 0.3 | |
| Frequency weightings | A | Pass | 0.3 | |
| | С | Pass | 0.3 | |
| | Lin | Pass | 0.3 | |
| Time weightings | Single Burst Fast | Pass | 0.3 | |
| 5 5 | Single Burst Slow | Pass | 0.3 | |
| Peak response | Single 100µs rectangular pulse | N/A | N/A | |
| R.M.S. accuracy | Crest factor of 3 | Pass | 0.3 | |
| Time weighting I | Single burst 5 ms at 2000 Hz | Pass | 0.3 | |
| | Repeated at frequency of 100 Hz | Pass | 0.3 | |
| Time averaging | 1 ms burst duty factor 1/10 ³ at 4kHz | Pass | 0.3 | |
| | 1 ms burst duty factor 1/10 ⁴ at 4kHz | Pass | 0.3 | |
| Pulse range | Single burst 10 ms at 4 kHz | Pass | 0.4 | |
| Sound exposure level | Single burst 10 ms at 4 kHz | Pass | 0.4 | |
| Overload indication | SPL | Pass | 0.3 | |
| | Leq | Pass | 0.4 | |

Acoustic tests 2.

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

| Test: | Subtest | Status | Expanded Uncertanity (dB) | Coverage Factor |
|-------------------|---|--------------|------------------------------|--------------------|
| Acoustic response | Weighting A at 125 Hz Weighting A at 8000 Hz | Pass Pass | 0.3 0.5 | |

Response to associated sound calibrator 3.

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

| Λ | | - End - | 1 |
|----------------|---|-------------|-------------|
| Calibrated by: | ~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~ | Checked by: | h |
| · | Fung Chi Yip | | Lam Tze Wai |
| Date: | 21-Nov-2014 | Date: | 22-Nov-2014 |
| | U | | |

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co., Ltd.

Form No.CARP152-2/Issue 1/Rev C/01/02/2007

Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. 028 - CAL) under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific calibration activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation. Such terms of accreditation stipulate that the results shall be traceable to the International System of Units (S.I.) or recognised measurement standards. This certificate shall not be reproduced except in full.



G/F., 9/F., 12/F., 13/F. & 20/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. 香港遊竹坑道37,號利達中心地下,9根,12樓,13樓及20樓 E-mail: smac@cigismec.com Website: www.cigismec.com CIGISMEC

A CIGIS GROUP COMPANY

Tel : (852) 2873 6860 Fax : (852) 2555 7533

| Test Data for Sound | l Level M | eter | | | | Page 1 of 5 |
|---------------------|-----------|------|------------|---------|--------|----------------|
| Sound level mete | | 2250 | Serial No. | 2749852 | Date | 21-Nov-2014 |
| Microphone | type: | 4189 | Serial No. | 2695393 | Report | 14CA1120 03-01 |

SELF GENERATED NOISE TEST

The noise test is performed in the most sensitive range of the SLM with the microphone replaced by an equivalent impedance.

| Noise level in A weighting | 11.9 | dB |
|----------------------------|------|----|
| Noise level in C weighting | 14.0 | dB |
| Noise level in Lin | 20.0 | dB |

LINEARITY TEST

The linearity is tested relative to the reference sound pressure level using a continuous sinusoidal signal of frequency 4 kHz. The measurement is made on the reference range for indications at 5 dB intervals starting from the 94 dB reference sound pressure level. And until within 5 dB of the upper and lower limits of the reference range, the measurements shall be made at 1 dB intervals.(SLM set to LEQ/SPL)

| Reference/Expected level | Actua | level | Tolerance | Devia | tion |
|--------------------------|----------------|------------|-----------|----------------|------------|
| Reference/Expected level | non-integrated | integrated | | non-integrated | integrated |
| dB | dB | dB | +/- dB | dB | dB |
| 94.0 | 94.0 | 94.0 | 0.7 | 0.0 | 0.0 |
| 99.0 | 99.0 | 99.0 | 0.7 | 0.0 | 0.0 |
| 104.0 | 104.0 | 104.0 | 0.7 | 0.0 | 0.0 |
| 109.0 | 109.0 | 109.0 | 0.7 | 0.0 | 0.0 |
| 114.0 | 114.0 | 114.0 | 0.7 | 0.0 | 0.0 |
| 119.0 | 119.0 | 119.0 | 0.7 | 0.0 | 0.0 |
| 124.0 | 124.0 | 124.0 | 0.7 | 0.0 | 0.0 |
| 129.0 | 129.0 | 129.0 | 0.7 | 0.0 | 0.0 |
| 134.0 | 134.0 | 134.0 | 0.7 | 0.0 | 0.0 |
| 135.0 | 135.0 | 135.0 | 0.7 | 0.0 | 0.0 |
| 136.0 | 136.0 | 136.0 | 0.7 | 0.0 | 0.0 |
| 137.0 | 137.0 | 137.0 | 0.7 | 0.0 | 0.0 |
| 138.0 | 138.0 | 138.0 | 0.7 | 0.0 | 0.0 |
| 139.0 | 139.0 | 139.0 | 0.7 | 0.0 | 0.0 |
| 140.0 | 140.0 | 140.0 | 0.7 | 0.0 | 0.0 |
| 89.0 | 89.0 | 89.0 | 0.7 | 0.0 | 0.0 |
| 84.0 | 84.0 | 84.0 | 0.7 | 0.0 | 0.0 |
| 79.0 | 79.0 | 79.0 | 0.7 | 0.0 | 0.0 |
| 74.0 | 74.0 | 74.0 | 0.7 | 0.0 | 0.0 |
| 69.0 | 69.0 | 69.0 | 0.7 | 0.0 | 0.0 |
| 64.0 | 64.0 | 64.0 | 0.7 | 0.0 | 0.0 |
| 59.0 | 59.0 | 59.0 | 0.7 | 0.0 | 0.0 |
| 54.0 | 54.0 | 54.0 | 0.7 | 0.0 | 0.0 |
| 49.0 | 49.0 | 49.0 | 0.7 | 0.0 | 0.0 |

(c)Soils Materials Eng. Co., Ltd.

Form No.: CAWS 152/Issue 1/Rev. B/01/02/2007



G/F, 9/F, 12/F, 13/F. 8.20/F, Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. 香港资竹坑道37.號利達中心地下,9樓,12樓,13樓及20樓 E-mail: smec@cigismec.com Website: www.cigismec.com

CIGISMEC

Tel : (852) 2873 6860 Fax : (852) 2555 7533 A CIGIS GROUP COMPANY

| | | | Page 2 of 5 |
|-------|---------|------|-------------|
| l No. | 2749852 | Date | 21-Nov-2014 |

| Test Data | for Sound | Level Meter |
|-----------|-----------|-------------|
|-----------|-----------|-------------|

| Sound level me Microphone | eter type: type: | 2250 4189 | | Serial No. Serial No. | 2749852 2695393 | Dat | e 21-No | v-2014 |
|------------------------------|---------------------|--------------|------|--------------------------|--------------------|------|-------------|-----------|
| Microphone | type. | 4100 | | oona no. | 2000000 | Rej | oort: 14CA1 | 120 03-01 |
| 44.0 | | 44.0 | 44.0 | 0.7 | | 0.0 | 0.0 | |
| 39.0 | | 39.0 | 39.0 | 0.7 | | 0.0 | 0.0 | |
| 34.0 | | 34.0 | 34.0 | 0.7 | | 0.0 | 0.0 | |
| 33.0 | | 32.9 | 32.9 | 0.7 | | -0.1 | -0.1 | |
| 32.0 | | 31.9 | 31.9 | 0.7 | | -0.1 | -0.1 | |
| 31.0 | | 30.9 | 30.9 | 0.7 | 1 | -0.1 | -0.1 | |
| 30.0 | | 30.0 | 30.0 | 0.7 | L | 0.0 | 0.0 | j. |

Measurements for an indication of the reference SPL on all other ranges which include it

| Other ranges | Expected level | Actual level | Tolerance | Deviation |
|--------------|----------------|--------------|-----------|-----------|
| dB | dB | dB | +/- dB | dB |
| 20-140 | 94.0 | 94.0 | 0.7 | 0.0 |

Measurements on all level ranges for indications 2 dB below the upper limit and 2 dB above the lower limit

| Ranges | Reference/Expected level | Actual level | Tolerance | Deviation |
|--------|--------------------------|--------------|-----------|-----------|
| dB | dB | dB | +/- dB | dB |
| 00.140 | 30.0 | 30.0 | 0.7 | 0.0 |
| 20-140 | 138.0 | 138.0 | 0.7 | 0.0 |

FREQUENCY WEIGHTING TEST

The frequency response of the weighting netwoks are tested at octave intervals over the frequency ranges 31.5 Hz to 12500 Hz. The signal level at 1000 Hz is set to give an indication of the reference SPL. Frequency weighting A:

| Frequency | Ref. level | Expected level | Actual level | Tolerar | nce(dB) | Deviation |
|-----------------|------------|----------------|--------------|---------|---------|-----------|
| Hz | dB | dB | dB | + | - | dB |
| 1000.0 | 94.0 | 94.0 | 94.0 | 0.0 | 0.0 | 0.0 |
| 31.6 | 94.0 | 54.6 | 54.6 | 1.5 | 1.5 | 0.0 |
| 63.1 | 94.0 | 67.8 | 67.8 | 1.5 | 1.5 | 0.0 |
| 125.9 | 94.0 | 77.9 | 77.9 | 1.0 | 1.0 | 0.0 |
| 251.2 | 94.0 | 85.4 | 85.4 | 1.0 | 1.0 | 0.0 |
| 501.2 | 94.0 | 90.8 | 90.8 | 1.0 | 1.0 | 0.0 |
| 1995.0 | 94.0 | 95.2 | 95.2 | 1.0 | 1.0 | 0.0 |
| 3981.0 | 94.0 | 95.0 | 95.0 | 1.0 | 1.0 | 0.0 |
| 7943.0 | 94.0 | 92.9 | 92.9 | 1.5 | 3.0 | 0.0 |
| 12590.0 | 94.0 | 89.7 | 89.2 | 3.0 | 6.0 | -0.5 |
| Frequency weigh | ting C: | | | | | |
| Frequency | Ref. level | Expected level | Actual level | Tolerar | nce(dB) | Deviation |
| Hz | dB | dB | dB | + | - | dB |
| 1000.0 | 94.0 | 94.0 | 94.0 | 0.0 | 0.0 | 0.0 |
| 31.6 | 94.0 | 91.0 | 91.0 | 1.5 | 1.5 | 0.0 |

(c)Soils Materials Eng. Co., Ltd.

Form No.: CAWS 152/Issue 1/Rev. B/01/02/2007



G/F, 9/F, 12/F, 13/F. & 20/F, Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. 香港茵竹坑道3.7.號利蓬中心地下,9 楼,1 2 楼,1 3 楼及2 0 樱 E-mail: smec@cigismec.com Website: www.cigismec.com

CIGISMEC

Tel : (852) 2873 6860

Fax : (852) 2555 7533

A CIGIS GROUP COMPANY

Page 3 of 5

| Test Data | for | Sound | Level | Meter | |
|-----------|-----|-------|-------|-------|--|
|-----------|-----|-------|-------|-------|--|

| Sound level m Microphone | | /pe: pe: | 2250 4189 | | Serial No. Serial No. | | 9852 5393 | Date | 21-Nov-2014 |
|-----------------------------|-----|-------------|--------------|------|--------------------------|-----|--------------|--------|------------------|
| Microphone | (Å) | pe. | 4105 | | Cenarito. | 200 | 0000 | Report | : 14CA1120 03-01 |
| 63.1 | | 94.0 | | 93.2 | 93.2 | 1.5 | 1.5 | 0.0 | |
| 125.9 | : | 94.0 | | 93.8 | 93.8 | 1.0 | 1.0 | 0.0 | |
| 251.2 | | 94.0 | | 94.0 | 94.0 | 1.0 | 1.0 | 0.0 | |
| 501.2 | | 94.0 | i | 94.0 | 94.0 | 1.0 | 1.0 | 0.0 | |
| 1995.0 | i | 94.0 | | 93.8 | 93.8 | 1.0 | 1.0 | 0.0 | |
| 3981.0 | | 94.0 | | 93.2 | 93.2 | 1.0 | 1.0 | 0.0 | |
| 7943.0 | | 94.0 | Ļ | 91.0 | 91.0 | 1.5 | 3.0 | 0.0 | |
| 12590.0 | | 94.0 | | 87.8 | 87.3 | 3.0 | 6.0 | -0.5 | |

Frequency weighting Lin:

| Frequency | Ref. level | Expected level | Actual level | Tolera | nce(dB) | Deviation |
|-----------|------------|----------------|--------------|--------|---------|-----------|
| Hz | dB | dB | dB | + | - | dB |
| 1000.0 | 94.0 | 94.0 | 94.0 | 0.0 | 0.0 | 0.0 |
| 31.6 | 94.0 | 94.0 | 94.1 | 1.5 | 1.5 | 0.1 |
| 63.1 | 94.0 | 94.0 | 94.0 | 1.5 | 1.5 | 0.0 |
| 125.9 | 94.0 | 94.0 | 94.0 | 1.0 | 1.0 | 0.0 |
| 251.2 | 94.0 | 94.0 | 94.0 | 1.0 | 1.0 | 0.0 |
| 501.2 | 94.0 | 94.0 | 94.0 | 1.0 | 1.0 | 0.0 |
| 1995.0 | 94.0 | 94.0 | 94.0 | 1.0 | 1.0 | 0.0 |
| 3981.0 | 94.0 | 94.0 | 94.0 | 1.0 | 1.0 | 0.0 |
| 7943.0 | 94.0 | 94.0 | 94.0 | 1.5 | 3.0 | 0.0 |
| 12590.0 | 94.0 | 94.0 | 93.5 | 3.0 | 6.0 | -0.5 |

TIME WEIGHTING FAST TEST

Time weighting F is tested on the reference range with a single sinusoidal burst of duration 200 ms at a frequency 2000 Hz and an amplitude which produces an indication 4 dB below the upper limit of the primary indicator range when the signal is continuous. (Weight A, Maximum hold)

| Ref. level | Expected level Actual leve | | Tolerar | nce(dB) | Deviation | |
|------------|----------------------------|-------|---------|---------|-----------|--|
| dB | dB | dB | + | - | dB | |
| 116.0 | 115.0 | 115.0 | 1.0 | 1.0 | 0.0 | |

TIME WEIGHTING SLOW TEST

Time weighting S is tested on the reference range with a single sinusoidal burst of duration 500 ms at a frequency 2000 Hz and an amplitude which produces an indication 4 dB below the upper limit of the primary indicator range when the signal is continuous. (Weight A, Maximum hold)

| Ref. level | Expected level | Actual level | Tolera | nce(dB) | Deviation |
|------------|----------------|--------------|--------|---------|-----------|
| dB | dB | dB | + | - | dB |
| 116.0 | 111.9 | 111.9 | 1.0 | 1.0 | 0.0 |

RMS ACCURACY TEST

| The RMS detector accuracy is test | ted on the reference range for a crest factor of 3. | |
|-----------------------------------|---|--------------|
| Test frequency: | 2000 Hz | |
| Amplitude: | 2 dB below the upper limit of the primary indicator | range. |
| Burst repetition frequency: | 40 Hz | |
| Tone burst signal: | 11 cycles of a sine wave of frequency 2000 Hz. | (Set to INT) |

(c)Soils Materials Eng. Co., Ltd.

Form No.: CAWS 152/Issue I/Rev. B/01/02/2007



G/F., 9/F., 12/F., 13/F. & 20/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. 香港茵竹坑遒37.號利達中心地下,9樓,12樓,13樓及20樓 E-mail: smec@ciglismec.com Website: www.cigismec.com CIGISMEC

Tel : (852) 2873 6860

Fax : (852) 2555 7533

A CIGIS GROUP COMPANY

Page 4 of 5

Test Data for Sound Level Meter

| Sound level me | ter type: | 2250 | | Serial No. | 2749852 | Date | 21-Nov-2014 |
|----------------|----------------|------|----------------------|-------------------------------------|---------------------|-----------------|----------------|
| Microphone | type: | 4189 | | Serial No. | 2695393 | Report: | 14CA1120 03-01 |
| | | | | | | | |
| | Ref. Lev | /el | Expected level | Tone burst signal | Tolerance | Deviation | |
| Time wighting | Ref. Lev dB | /el | Expected level dB | Tone burst signal indication(dB) | Tolerance +/- dB | Deviation dB | |

TIME WEIGHTING IMPULSE TEST

Time weighting I is tested on the reference range (Set the SLM to LAImax)

Test frequency: 2000 Hz

Amplitude: The upper limit of the primary indicator range.

Single sinusoidal burst of duration 5 ms:

| Ref. Level | Single burs | t indication | Tolerance | Deviation |
|------------|---------------|--------------|-----------|-----------|
| dB | Expected (dB) | Actual (dB) | +/- dB | dB |
| 120.0 | 111.2 | 111.1 | 2.0 | -0.1 |

Repeated at 100 Hz

| Ref. Level | Repeated bu | irst indication | Tolerance | Deviation |
|------------|---------------|-----------------|-----------|-----------|
| dB | Expected (dB) | Actual (dB) | +/- dB | dB |
| 120.0 | 117.3 | 117.2 | 1.0 | -0.1 |

TIME AVERAGING TEST

This test compares the SLM reading for continuous sine signals with readings obtained from a sine tone burst sequence having the same RMS level. The test level is 30 dB below the upper limit of the linearity range and repeated for Type 1 SLM with 40 dB below the upper limit of the linearity.

Frequency of tone burst: 4000 Hz

| Duration of tone burst: | 1 ms | | | | | |
|-------------------------|------------|----------|--------|-----------|-----------|--------------|
| Repetition Time | Level of | Expected | Actual | Tolerance | Deviation | Remarks |
| | tone burst | Leq | Leq | | | |
| msec | dB | dB | dB | +/- dB | dB | |
| 1000 | 110.0 | 110.0 | 109.9 | 1.0 | -0.1 | 60s integ. |
| 10000 | 100.0 | 100.0 | 99.9 | 1.0 | -0.1 | 6min. integ. |

PULSE RANGE AND SOUND EXPOSURE LEVEL TEST

10 sec

The test tone burst signal is superimposed on a baseline signal corresponding to the lower limit of reference rar Test frequency: 4000 Hz

Integration time:

The integrating sound level meter set to Leq:

| Duration | Rms level of | Expected | Actual | Tolerance | Deviation |
|----------|-----------------|----------|--------|-----------|-----------|
| msec | tone burst (dB) | dB | dB | +/- dB | dB |
| 10 | 120.0 | 90.0 | 90.0 | 1.7 | 0.0 |

The integrating sound level meter set to SEL:

| Duration | Rms level of | Expected | Actual | Tolerance | Deviation |
|----------|-----------------|----------|--------|-----------|-----------|
| msec | tone burst (dB) | dB | dB | +/- dB | dB |
| 10.0 | 120.0 | 100.0 | 100.0 | 1.7 | 0.0 |

(c)Soils Materials Eng. Co., Ltd.

Form No.: CAWS 152/issue 1/Rev, B/01/02/2607



G/F., 9/F., 12/F., 13/F. & 20/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong, 音 推 實 作 抗 道 3.7.號 利 達 中心 地下, 9 想, 1 2 櫻、 [3 櫻 及 2 0 櫻 E-mail: smec@cigismec.com Website: www.cigismec.com CIGISMEC

A CIGIS GROUP COMPANY

Tel : (852) 2873 6860

Fax : (852) 2555 7533

| Test Data for Sound Level M | eter | | | | Page 5 of 5 |
|-----------------------------|------|------------|---------|--------|----------------|
| Sound level meter type: | 2250 | Serial No. | 2749852 | Date | 21-Nov-2014 |
| Microphone type: | 4189 | Serial No. | 2695393 | Report | 14CA1120 03-01 |

OVERLOAD INDICATION TEST

| Test frequer | ncy: | non-integrating m 2000 Hz | | | |
|--------------|------------------|------------------------------|--------------------|-------------------|-----------------|
| Amplitude: | | 2 dB below the up | per limit of the p | nmary indicator r | ange. |
| • | | 40 Hz | | | |
| Tone burst s | lanalı | 11 cycles of a sine | a wave of freque | | |
| Tone pursus | agnai: | TT Cycles Ut a sin | e wave of neque | Incy 2000 Hz. | |
| Level | Level reduced by | | Difference | Tolerance | Deviation |
| | 1 | | | | Deviation dB |

For integrating SLM, with the instrument indicating Leq.

| | | | | | ange. The test signal as the lower limit of refere |
|------------------|------------------|----------------|-----------------|---------------------|---|
| Test frequer | - | 4000 Hz | buconno orginar | oon oop on an ig to | |
| Integration t | , | 10 sec | | | |
| Single burst | duration: | 1 msec | | | |
| Rms level | Level reduced by | Expected level | Actual level | Tolerance | Deviation |
| at overload (dB) | 1 dB | dB | dB· | dB | dB |
| 140.9 | 139.9 | 99.9 | 99.9 | 2.2 | 0.0 |

ACOUSTIC TEST

The acoustic test of the complete SLM is tested at the frequency 125 Hz and 8000 Hz using a B&K type 4226 Multifunction Acoustic Calibrator. The test is performed in A weighting.

| Frequency | Expected level | Actual level | Toleran | ce (dB) | Deviation |
|-----------|----------------|---------------|---------|---------|-----------|
| Hz | dB | Measured (dB) | + | - | dB |
| 1000 | 94.0 | 94.0 | 0.0 | 0.0 | 0.0 |
| 125 | 77.9 | 77.8 | 1.0 | 1.0 | -0.1 |
| 8000 | 92.9 | 93.2 | 1.5 | 3.0 | 0.3 |

-----END------

(c)Soils Materials Eng. Co., Ltd.

Form No.: CAWS 152/Issue 1/Rev. B/01/02/2007



綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. Gr. gr. 12rf. 12rf. 13rf. 8 20rf. Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. 香港黄竹坑道37號利達中心地下,9樓,12樓,13樓及20樓 E-mail: smec@cigismec.com Website: www.cigismec.com

Tel : (852) 2873 6860 Fax : (852) 2555 7533



CERTIFICATE OF CALIBRATION

| | 14CA1120 03-03 | | Page: | |
|--|---|--|--|---|
| Item tested | | | | |
| Description: | Acoustical Calibrat | or (Class 1) | | |
| Manufacturer: | B & K | , | | |
| Type/Model No.: | 4231 | | | |
| Serial/Equipment No.: | 1795386 | | | |
| Adaptors used: | - | | | |
| Item submitted by | | | | |
| Curstomer: | MTR Corporation I | imited | | |
| Address of Customer: | - | | | |
| Request No.: | - | | | |
| Date of receipt: | 20-Nov-2014 | | | |
| Date of test: | 21-Nov-2014 | 1999 Y 1 (1997 - 197 - 19 - 1 | | |
| | | 88 | | |
| Reference equipment | used in the calib | ration | | |
| Description: | Model: | Serial No. | Expiry Date: | Traceable to: |
| Lab standard microphone | B&K 4180 | 2412857 2743150 | 13-May-2015 | SCL CEPREI |
| Preamplifier Meanwing amplifier | B&K 2673 | | 10-Apr-2015 08-Apr-2015 | CEPREI |
| Measuring amplifier | B&K 2610 DS 360 | 2346941 61227 | 08-Apr-2015 09-Apr-2015 | CEPREI |
| Signal generator Digital multi-meter | 34401A | 01227 US36087050 | 17-Dec-2014 | CEPREI |
| Audio analyzer | 8903B | GB41300350 | 07-Apr-2015 | CEPREI |
| Universal counter | 53132A | MY40003662 | 11-Apr-2015 | CEPREI |
| Ambient conditions | | | | |
| Temperatura | 21 ± 1 °C | | | |
| Temperature: Relative humidity: | 60 ± 10 % | | | |
| Air pressure: | 1010 ± 10 hPa | | | |
| | | | | |
| · | | · ··· • ··· • ···· • · ··· • · · · · · | | |
| Test specifications | | | | |
| Test specifications 1, The Sound Calibrato | | | requirements as specif | ied in IEC 60942 1997 Annes |
| Test specifications 1, The Sound Calibrato and the lab calibratio | n procedure SMTP00 | 4-CA-156. | | ied in IEC 60942 1997 Annex y using insert voltage techniq |
| Test specifications 1. The Sound Calibrato and the lab calibratio 2. The calibrator was le | on procedure SMTP00 ested with its axis vert | 4-CA-156. ical facing downwards a | at the specific frequency | y using insert voltage techniq |
| Test specifications 1, The Sound Calibrato and the lab calibratio 2, The calibrator was te 3, The results are round | on procedure SMTP00 ested with its axis vert ded to the nearest 0.0 | 4-CA-156. ical facing downwards a 11 dB and 0.1 Hz and ha | at the specific frequency | |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 | on procedure SMTP00 ested with its axis vert ded to the nearest 0.0 | 4-CA-156. ical facing downwards a 11 dB and 0.1 Hz and ha | at the specific frequency | y using insert voltage techniq for variations from a reference |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. Test results This is to certify that the sound c | In procedure SMTPOC ested with its axis vert ded to the nearest 0.0 hectoPascals as the calibrator conforms to the | 4-CA-156. ical facing downwards a 11 dB and 0.1 Hz and ha maker's information ind e requirements of annex B | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the | y using insert voltage techniq for variations from a reference nt is insensitive to pressure |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. | In procedure SMTPOC ested with its axis vert ded to the nearest 0.0 hectoPascals as the calibrator conforms to the | 4-CA-156. ical facing downwards a 11 dB and 0.1 Hz and ha maker's information ind e requirements of annex B | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the | y using insert voltage techniq for variations from a reference nt is insensitive to pressure |
| Test specifications 1, The Sound Calibrato and the lab calibratio 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. Test results This is to certify that the sound of | on procedure SMTP00 ested with its axis vert ded to the nearest 0.0 hectoPascals as the hectoPascals as the calibrator conforms to the es not imply that the s | 4-CA-156. ical facing downwards a 11 dB and 0.1 Hz and hi maker's information ind evenue of annex B ound calibrator meets I | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the EC 60942 under any of | y using insert voltage techniq for variations from a reference nt is insensitive to pressure |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. Test results This is to certify that the sound of test was performed. This doe | on procedure SMTP00 ested with its axis vert ded to the nearest 0.0 hectoPascals as the hectoPascals as the calibrator conforms to the es not imply that the s | 4-CA-156. ical facing downwards a 11 dB and 0.1 Hz and hi maker's information ind evenue of annex B ound calibrator meets I | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the EC 60942 under any of | y using insert voltage techniq for variations from a reference nt is insensitive to pressure |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. Test results This is to certify that the sound of test was performed. This doe | on procedure SMTP00 ested with its axis vert ded to the nearest 0.0 hectoPascals as the hectoPascals as the calibrator conforms to the es not imply that the s | 4-CA-156. ical facing downwards a 11 dB and 0.1 Hz and hi maker's information ind evenue of annex B ound calibrator meets I | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the EC 60942 under any of certificate. | y using insert voltage techniq for variations from a reference nt is insensitive to pressure e conditions under which the her conditions. |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. Test results This is to certify that the sound of test was performed. This doe Details of the performed meas Approved Signatory: | on procedure SMTP00 ested with its axis vert ded to the nearest 0.0 hectoPascals as the hectoPascals as the calibrator conforms to the es not imply that the s | 4-CA-156. ical facing downwards a 11 dB and 0.1 Hz and hi maker's information ind e requirements of annex B ound calibrator meets I inted on page 2 of this Date: 22-Nov- | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the EC 60942 under any of certificate. | y using insert voltage techniq for variations from a reference nt is insensitive to pressure e conditions under which the her conditions. |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. Test results This is to certify that the sound o test was performed. This doe Details of the performed mea | on procedure SMTPOC ested with its axis vert ded to the nearest 0.0 hectoPascals as the calibrator conforms to the est not imply that the s asurements are prese | 4-CA-156. ical facing downwards a 1 dB and 0.1 Hz and hi maker's information ind e requirements of annex B ound calibrator meets I inted on page 2 of this Date: 22-Nov-2 i e refer to the conditon o | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the EC 60942 under any of certificate. 2014 Company C | y using insert voltage techniq for variations from a reference in is insensitive to pressure a conditions under which the her conditions. |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. Test results This is to certify that the sound c test was performed. This doe Details of the performed mea Approved Signatory: Hu Comments: The results repute | on procedure SMTPOC ested with its axis vert ded to the nearest 0.0 hectoPascals as the calibrator conforms to the est not imply that the s asurements are prese | 4-CA-156. ical facing downwards a 1 dB and 0.1 Hz and hi maker's information ind e requirements of annex B ound calibrator meets I inted on page 2 of this Date: 22-Nov-2 i e refer to the conditon o | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the EC 60942 under any of certificate. 2014 Company C | y using insert voltage techniq for variations from a reference in is insensitive to pressure a conditions under which the her conditions. |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. Test results This is to certify that the sound c test was performed. This doe Details of the performed meas Approved Signatory: Hui Comments: The results repute | an procedure SMTPOC ested with its axis vert ded to the nearest 0.0 hectoPascals as the calibrator conforms to the estimator conformator conformator estimator conformator estimator estimator conformator estimator conformator estimator estimator conformator estimator est | 4-CA-156. ical facing downwards a 1 dB and 0.1 Hz and hi maker's information ind e requirements of annex B ound calibrator meets I inted on page 2 of this Date: 22-Nov-2 i e refer to the conditon o | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the EC 60942 under any ot certificate. 2014 Company C f the instrument on the | y using insert voltage techniq for variations from a reference in is insensitive to pressure a conditions under which the her conditions. |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. Test results This is to certify that the sound of test was performed. This doe Details of the performed mea Approved Signatory: Hui Comments: The results repr carry no implication regarding to Solis & Materials Engineering Co., Ltd. | on procedure SMTPOC ested with its axis vert ded to the nearest 0.0 hectoPascals as the calibrator conforms to the est not imply that the s asurements are prese and Jien Min/Feng Jun 0 orted in this certificate ig the long-term stabil | 4-CA-156. ical facing downwards a 1 dB and 0.1 Hz and hi maker's information ind a requirements of annex B ound calibrator meets I inted on page 2 of this Date: 22-Nov-2 a refer to the conditon o ity of the instrument. | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the EC 60942 under any ot certificate. 2014 Company C f the instrument on the Form b | y using insert voltage techniq for variations from a reference in is insensitive to pressure a conditions under which the her conditions. |
| Test specifications 1, The Sound Calibrato and the lab calibrato 2, The calibrator was te 3, The results are round pressure of 1013.25 changes. Test results This is to certify that the sound c test was performed. This doe Details of the performed mea Approved Signatory: Hui Comments: The results repr carry no implication regarding | on procedure SMTPOC ested with its axis vert ded to the nearest 0.0 hectoPascals as the calibrator conforms to the estimator conforms to the estimator conforms to the estimator conforms to the sourcements are prese and Jion Min/Feng Jun 0 orted in this certificate ig the long-term stabil | 4-CA-156. ical facing downwards a 1 dB and 0.1 Hz and hi maker's information ind e requirements of annex B ound calibrator meets I inted on page 2 of this Date: 22-Nov-2 a e refer to the conditon o ity of the instrument. laboratory (Reg. No. 0 | at the specific frequency ave not been corrected icates that the instrume of IEC 60942: 1997 for the EC 60942 under any ot certificate. 2014 Company C f the instrument on the Form N 28 - CAL) under the Ho | y using insert voltage techniq for variations from a reference in is insensitive to pressure a conditions under which the her conditions. |



G/F. 9/F., 12/F., 13/F. & 20/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. 香港黃竹坑道37號利達中心地下,9樓,12樓,13樓及20樓 E-mail: smec@cigismec.com Website: www.cigismec.com

14CA1120 03-03



CERTIFICATE OF CALIBRATION (Continuation Page)

(continuation rage)

Page: 2 of

2

Tel : (852) 2873 6860 Fax : (852) 2555 7533

1, Measured Sound Pressure Level

Certificate No.:

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

| Frequency | Output Sound Pressure | Measured Output | Estimated Expanded |
|-----------|-----------------------|----------------------|--------------------|
| Shown | Level Setting | Sound Pressure Level | Uncertainty |
| Hz | dB | dB | dB |
| 1000 | 94.00 | 93.88 | 0.10 |

2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be:

| At 1000 Hz | STF = 0.002 dB |
|--------------------------------|----------------|
| Estimated expanded uncertainty | 0.005 dB |

3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

| At 1000 Hz | Actual Frequency = 999.8 Hz | |
|--------------------------------|-----------------------------|-------------------------|
| Estimated expanded uncertainty | 0.1 Hz | Coverage factor k = 2.2 |

4, Total Noise and Distortion

factor of 2 is assumed unless explicitly stated.

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

| At 1000 Hz | TND = 0.4 % |
|--------------------------------|-------------|
| Estimated expanded uncertainty | 0.7 % |


The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage


| | Λ | , | - | End - | 1 - | |
|----------------|---|--------------|---|-------------|----------------------------|---|
| Calibrated by: | 5 | \sim | | Checked by: | h | _ |
| Date: | | Fung Chi Yip | | Date: | Lam Tze Wai 22-Nov-2014 | |
| Dute | | 11101-2014 | | | EL HOT LOTT | |


The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.


| © Soits & Materials Engineering Co., Ltd. | Form No.CARP155-2/Issue 1/Rev.C/01/05/2005 |
|--|--|
| Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. 028 - CAL) under th | e Hong Kong Laboratory Accreditation Scheme |
| (HOKLAS) for specific calibration activities as listed in the HOKLAS Directory of Accredited Laborator | ies. The results shown in this certificate were |
| determined by this laboratory in accordance with its terms of accreditation. Such terms of accreditation s | stipulate that the results shall be traceable to the |
| International System of Units (S.L) or recognised measurement standards. This certificate | a shall not be reproduced except in full. |

<u>Appendix F</u> <u>Impact Monitoring Graphical Plots</u>

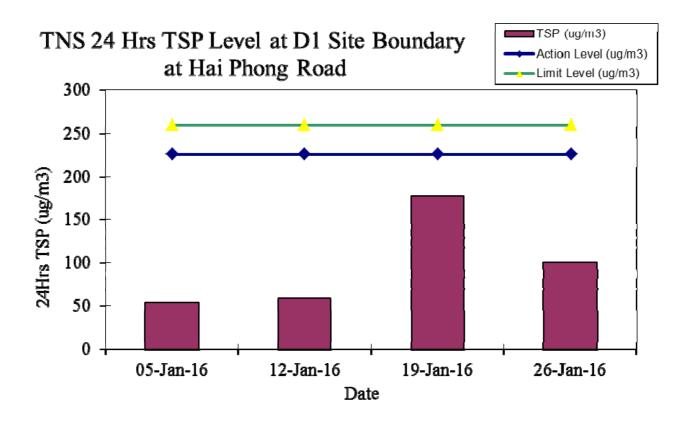

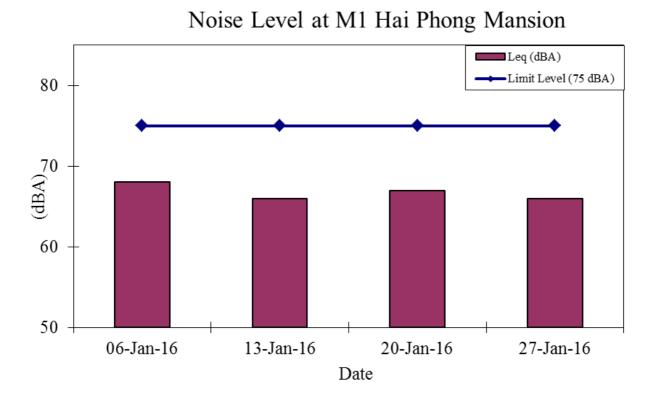

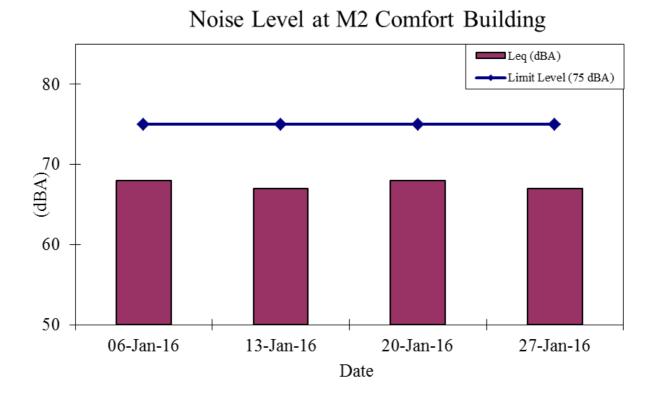

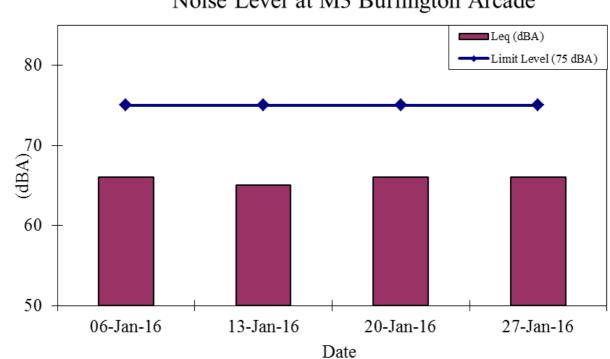

Noise Level at M3 Burlington Arcade

<u>Appendix G</u> <u>Monitoring Schedule for the Present and Next</u> <u>Reporting Period</u>

| Monitoring Schedule for January 2016 | | | |
|--------------------------------------|-----------------|-----------------|-----------------|
| Dust | Noise | | |
| D1 | M1 | M2 | M3 |
| 5 January 2016 | 6 January 2016 | 6 January 2016 | 6 January 2016 |
| 12 January 2016 | 13 January 2016 | 13 January 2016 | 13 January 2016 |
| 19 January 2016 | 20 January 2016 | 20 January 2016 | 20 January 2016 |
| 26 January 2016 | 27 January 2016 | 27 January 2016 | 27 January 2016 |

| Monitoring Schedule for February 2016 | | | | |
|---------------------------------------|------------------|------------------|------------------|--|
| Dust | Noise | | | |
| D1 | M1 | M2 | M3 | |
| 2 February 2016 | 3 February 2016 | 3 February 2016 | 3 February 2016 | |
| 12 February 2016 | 12 February 2016 | 12 February 2016 | 12 February 2016 | |
| 16 February 2016 | 16 February 2016 | 16 February 2016 | 16 February 2016 | |
| 23 February 2016 | 24 February 2016 | 24 February 2016 | 24 February 2016 | |

Remarks:

The schedule may be changed due to unforeseen circumstances (adverse weather, etc)
