


Sun Fook Kong – Bestwise Joint Venture

Contract No. DC/2009/10 HATS Stage 2A – Upgrading Works at Stonecutters Island Sewage Treatment Works - Main Pumping Station, Sedimentation Tanks and Ancillary Facilities

Quarterly Environmental
Monitoring and Audit Report
April to June 2020

(Version 1.0)

Certified By 
(Environmental Team Leader)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

WELLAB accepts no responsibility for changes made to this report by third parties

WELLAB LTD
Room 1701, Technology Park,
18 On Lai Street,
Shatin, NT, Hong Kong
Tel: (852) 2898 2083 Fax: (852) 2898 7076
Email: info@wellab.com.hk

CE/Harbour Area Treatment Scheme
Drainage Services Department
Sewage Services Branch
Harbour Area Treatment Scheme Division
c-/ G/F, Western Magistracy
2A Pokfulam Road, Hong Kong

Attn: Mr. K K Kam

**Agreement No. CE 8/2009(EP) Harbour Area Treatment Scheme Stage 2A
Independent Environmental Checker for Construction Phase – Investigation**

Our Reference
EC/AFK/DC/jj/
T261332/22.01/L-1460

**Contract No. DC/2009/10 – Upgrading Works at Stonecutters Island Sewage
Treatment Works – Main Pumping Station, Sedimentation Tanks and Ancillary
Facilities**

3/F International Trade
Tower
348 Kwun Tong Road
Kowloon
Hong Kong

Submission of 37th Quarterly EM&A Report for April to June 2020 (v1.0)

T +852 2828 5757
F +852 2827 1823
mottmac.hk

17 August 2020

By Post

Dear Sir,

We refer to the captioned Quarterly EM&A Report for April to June 2020 (v1.0)
received on 11 August 2020 and we confirm that we have no comment.

Yours faithfully
for MOTT MACDONALD HONG KONG LIMITED



Ir Dr Anne F Kerr
Independent Environmental Checker
T +852 2828 5757
anne.kerr@mottmac.com

c.c.

Ove Arup & Partners HK Limited
Sun Fook Kong – Bestwise Joint Venture
Wellab Limited

Mr. Mark Ngan
Mr. Keith Ho
Dr. Priscilla Choy

Fax: 2370 4377
By email
By email

TABLE OF CONTENTS

	Page
EXECUTIVE SUMMARY	1
Introduction	1
Environmental Monitoring Works	2
Environmental Licenses and Permits	3
Environmental Mitigation Implementation Schedule	3
Key Information in the Reporting Quarter	3
Summary of Complaints and Prosecutions	3
1. INTRODUCTION	4
Background	4
Project Organizations	4
Summary of EM&A Requirements	5
2. AIR QUALITY	6
Monitoring Requirements	6
Monitoring Locations	6
Monitoring Parameters, Frequency and Duration	6
Monitoring Methodology and QA/QC Procedure	6
Results and Observations	6
3. NOISE.....	7
Monitoring Requirements	7
Monitoring Locations	7
Monitoring Parameters, Frequency and Duration	7
Monitoring Methodology and QA/QC Procedures	7
Results and Observations	7
4. ENVIRONMENTAL AUDIT	9
Site Audits	9
Review of Environmental Monitoring Procedures	9
Status of Environmental Licensing and Permitting	9
Waste Management Status	9
Implementation Status of Event Action Plans	11
Summary of Complaints and Prosecutions	11
5. FUTURE KEY ISSUES	12
Key Issues for the Coming Months	12
Construction Program for the Coming Quarter	12
6. CONCLUSIONS AND RECOMMENDATIONS	13
Conclusions	13
Recommendations for the coming reporting period:	13

LIST OF TABLES

Table I	Summary Table for Non-compliance Recorded in the Reporting Quarter
Table II	Summary Table for Key Information in the Reporting Quarter
Table 1.1	Key Project Contacts
Table 2.1	Locations for Air Quality Monitoring
Table 2.2	Impact Dust Monitoring Parameters, Frequency and Duration
Table 3.1	Locations for Noise Monitoring Stations
Table 3.2	Noise Monitoring Parameters, Frequency and Duration
Table 4.1	Summary of Environmental Licensing and Permit Status
Table 4.2a-c	Observations and Recommendations of Site Audits

LIST OF FIGURES

Figure 1	General Location Plan of the Project and Locations of Air Quality and Noise Monitoring Stations
Figure 2	ET's Organization Chart

LIST OF APPENDICES

A	Action and Limit Levels for Air Quality and Noise
B	Summary of Exceedance
C	1-hour and 24-hour TSP Monitoring Graphical Presentations
D	Noise Monitoring Graphical Presentations
E	Summary of Amount of Waste Generated
F	Event Action Plans
G	Environmental Mitigation Implementation Schedule (EMIS)
H	Complaint Log
I	Construction Programme

ABBREVIATION AND ACRONYM

AL Levels	Action and Limit Levels
DSD	Drainage Services Department
E / ER	Engineer/Engineer's Representative
EIA	Environmental Impact Assessment
EM&A	Environmental Monitoring and Audit
EMIS	Environmental Mitigation Implementation Schedule
EP	Environmental Permit
EPD	Environmental Protection Department
ET	Environmental Team
HVS	High Volume Sampler
IEC	Independent Environmental Checker
RE	Resident Engineer
RH	Relative Humidity
QA/QC	Quality Assurance / Quality Control
SLM	Sound Level Meter
WMP	Waste Management Plan
SCISTW	Stonecutters Island Sewage Treatment Works
HATS Stage 2A	Harbour Area Treatment Scheme Stage 2A
SBJV	Sun Fook Kong - Bestwise Joint Venture

EXECUTIVE SUMMARY

Introduction

1. This is the 37th Quarterly Environmental Monitoring and Audit (EM&A) Report prepared by Wellab Limited for DSD Contract No. DC/2009/10 “HATS Stage 2A – Upgrading Works at Stonecutters Island Treatment Works – Main Pumping Station, Sedimentation Tanks and Ancillary Facilities” (The Project) which documents the key information of EM&A and environmental monitoring works undertaken at the SCISTW under HATS Stage 2A Environmental Permit (Permit No. EP-322/2008/G).
2. The site activities undertaken in the reporting quarter included:

April 2020:

MPS2

- Parallel operation with DSD/ST2 completed on 16 Feb 2020, but support for maintenance of Fire service and lift service extended one more month to 16 Mar 2020.
- DOU3 upgrading works – BTF#3 upgrade completed. SWAC for temporary suspension of extraction fan for BTF#2 upgrading works was received on 25 Mar. Set up of temporary carbon filter connecting to wet well vent pipe at Maintenance Hall per ST2’s requested is on-going.
- Base line test for Main Pump #1 to 4 on-going.
- Defects rectification (on-going).
- Expert System, SAT of Disinfection, Sludge Dewatering and DOU on-going.
- A/C VRV set #2 & #4 and PAU 1-3 replacement in progress.
- Installation of FRP Platform at B1 of Wet Well Pipe Shaft of Main Pumping Station No.2

NaOCl Compound

- Dosing pump 503 below capacity issue was resolved.
- RT 4-day trail run started on 10 Mar 2020 (Tue) was ceased due to minor programme bug. Target to resume the RT on 16 Apr 2020.

CEPT

- Pre-handover inspection, maintenance and defect rectification for FT5 and PSTs (PST47/49, 51/53, 48/50 & 52/54) (on-going).

May 2020:

MPS2

- DOU3 upgrading works – BTF#2 upgrading works in progress. Currently 2 sets of temporary carbon filter tanks are connected for discharge air polishing.
- Base line test for Main Pump #1 to 4 on-going. (except #2). Further shut off head test requested by Kubota being arranged.
- Defects rectification (on-going).
- Expert System DSS development in progress.
- A/C VRV set #2 & #4 and PAU 1-3 replacement completed.

NaOCl Compound

- RT for NaOCl dosing system commenced on 6 May 2020, target to complete on 5 June

CEPT

- Pre-handover inspection, maintenance and defect rectification for FT5 and PSTs (PST47/49, 51/53, 48/50 & 52/54) (on-going).

June 2020:MPS2

- DOU3 upgrading works – BTF#2 installation completed and seeding underway. In addition to previously 2 temp carbon filter tanks, 2 more were instructed to be provided for discharge air polishing.
- Base line test for Main Pump #1 to 4 on-going. (except #2). Shut off head test requested by Kubota is on-going.
- Defects rectification (on-going).
- Expert SystemDSS development in progress.
- Pre-handover inspection for Inlet Chamber and Valve Chamber.

CEPT

- Pre-handover inspection, maintenance and defect rectification for FT5 and PSTs (PST47/49,51/53, 48/50 & 52/54) (on-going).

Environmental Monitoring Works

- The environmental monitoring works conducted for the Project in this reporting quarterly period at air quality monitoring stations AM6a and noise monitoring stations NM5. Alternative location for AM6 was adopted in January 2016 as AM6a.
- All the environmental monitoring works were conducted in accordance with the EM&A Manual. The monitoring results were checked and reviewed. Site audits were conducted once per week. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.
- Summary of the non-compliance of the reporting quarter is tabulated in **Table I**.

Table I Summary Table for Non-compliance Recorded in the Reporting Quarter

Monitored By	Monitoring Station	Parameter	No. of Exceedance		No. of Exceedance Due to the Project		Action Taken
			Action Level	Limit Level	Action Level	Limit Level	
DC/2009/10	AM6a (*)	1-hr TSP	0	0	0	0	N/A
		24-hr TSP	0	0	0	0	N/A
	NM5	Noise	0	0	0	0	N/A
	NM6	Noise	0	0	0	0	N/A
	AM7	1-hr TSP	0	0	0	0	N/A
		24-hr TSP	0	0	0	0	N/A
	AM8	1-hr TSP	0	0	0	0	N/A
		24-hr TSP	0	0	0	0	N/A

Remark

(*) Alternative location for AM6 was adopted in January 2016 as AM6a (Please refer to Section 2.2).

1-hour TSP Monitoring

- All 1-hour TSP monitoring was conducted as scheduled in the reporting quarter. No Action/Limit Level exceedance was recorded.

24-hour TSP Monitoring

- All 24-hour TSP monitoring was conducted as scheduled in the reporting quarter. No Action/Limit Level exceedance was recorded.

Construction Noise

8. All construction noise monitoring was conducted as scheduled in the reporting quarter. No Action/Limit Level exceedance was recorded.

Environmental Licenses and Permits

9. Licenses/Permits granted to the Project include the Environmental Permit (EP); Billing account for Disposal of Construction Waste, Registered as Chemical Waste Producer and Construction Noise Permits.

Environmental Mitigation Implementation Schedule

10. According to the EIA Report Section 3.74, 4.56 and 13.44, air quality, noise and landscape and visual would be the key environmental issues and mitigation measures shall be implemented during the construction phase. Details of the implementation of mitigation measures are provided in the **Appendix G**.

Key Information in the Reporting Quarter

11. Summary of key information in the reporting quarter is tabulated in **Table II**.

Table II Summary Table for Key Information in the Reporting Quarter

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Complaint received	0	---	N/A	N/A	---
Status of submissions covering the reporting quarter	3	Monthly EM&A Reports from March to May 2020	Submitted to IEC for verification	No Comment	---
Notifications of any summons & prosecutions received	0	---	N/A	N/A	---

Summary of Complaints and Prosecutions

12. No environmental complaint and prosecution was received for the Project in the reporting quarter.
13. There were no environmental complaint and prosecution received since the commencement of the Project. The Complaint Log is presented in **Appendix H**.
14. The environmental concerns in the coming months are mainly on construction waste and general refuse storage.

1. INTRODUCTION

Background

- 1.1 The Project ‘HATS Stage 2A - Upgrading works at Stonecutters Island Treatment Works – Main Pumping Station, Sedimentation Tanks and Ancillary Facilities’ under Contract No: DC/2009/10 mainly comprises the construction of a large underground pumping station with an internal diameter of 55 metres and a depth of more than 40 metres, the provision of additional double-tray sedimentation tanks, a new computer control system, the expansion and modification of existing installations of the SCISTW as well as the construction of other ancillary facilities. The general location plan of the Project is shown in **Figure 1**.
- 1.2 The Project is under Harbour Area Treatment Scheme (HATS) Stage 2A and is a designated project with Register No. : AEIAR-121/2008. The current works under the Project at SCISTW for HATS 2A is covered by Environmental Permit (Permit No. EP-322/2008/G), which was issued on 9th May 2014 by the Environmental Protection Department (hereinafter called EPD) to the Drainage Services Department (hereinafter called the DSD) as the Permit Holder.
- 1.3 Since the Contracts DC/2009/05, DE/2009/02 and DC/2007/23 in the SCISTW had been substantial completed, the environmental monitoring works at NM5, NM6, AM6, AM7 and AM8 have since been handed over to the ET of DC/2009/10 from August and September 2012.
- 1.4 Sun Fook Kong -Bestwise Joint Venture (hereafter called the SBJV) was commissioned by the DSD to undertake the construction of the Contract No.DC/2009/10 “HATS 2A – Upgrading works at Stonecutters Island Treatment Works – Main Pumping, Sedimentation Tanks and Ancillary Facilities”. The date of commencement of construction of the Project is 24th February 2011. There was a change of name of the Joint Venture from Sun Fook Kong – Biwater Joint Venture to Sun Fook Kong – Bestwise Joint Venture with effect from 30 November 2018.
- 1.5 Cinotech Consultants Limited was commissioned by SBJV to undertake the Environmental Monitoring and Audit (EM&A) works for the project and was appointed as the Environmental Team (ET) of the Project under Condition 2.1 of the EP. The ET of this project was taken over by Wellab Limited (Wellab) starting from 1st January 2019.
- 1.6 The date of commencement of EM&A works is 14th April 2011.

Project Organizations

- 1.7 The contacts of the Project are shown in **Table 1.1** and the organization chart of ET for Contract is shown in **Figure 2**.

Table 1.1 Key Project Contacts

Party	Role	Name	Position	Phone No.
Ove Arup & Partners Hong Kong Ltd	Engineer’s Representative	Mr. Ted Tang	Principle Resident Engineer	2370 4311
		Mr. Tony Yeung	ER’s Coordinator	6049 5562

Party	Role	Name	Position	Phone No.
Wellab	Environmental Team	Dr. Priscilla Choy	ET Leader	2151 2089
		Mr. Howard Chan	Project Coordinator	2151 2073
Mott MacDonald	Independent Environmental Checker	Dr. Anne Kerr	Independent Environmental Checker	2828 5757
Sun Fook Kong - Bestwise Joint Venture	Contractor	Mr. Keith Ho	Site Agent	2620 0070
		Mr. Albus Cheung	Environmental Officer	2620 0070

Summary of EM&A Requirements

- 1.8 The EM&A programme requires construction phase monitoring for air quality and construction noise, landscape and visual and environmental site audit. The EM&A requirements for each parameter are described in the following sections, including:
- All monitoring parameters;
 - Action and Limit levels for all environmental parameters;
 - Event Action Plans;
 - Environmental mitigation measures, as recommended in the project EIA study final report; and
 - Environmental requirements in contract documents.
- 1.9 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in **Section 4** of this report.
- 1.10 This report presents the monitoring results, observations, locations, equipment, period, for required monitoring parameter namely air quality, noise and audit works conducted for the Project for April to June 2020.

2. AIR QUALITY

Monitoring Requirements

- 2.1 1-hour and 24-hour TSP monitoring were conducted to monitor the air quality. **Appendix A** shows the established Action/Limit Levels for the environmental monitoring works.

Monitoring Locations

- 2.2 Three designated monitoring stations, AM6a, AM7 and AM8 were selected for impact dust monitoring for the Project. The original location of AM6 was inaccessible due to planned construction works and therefore an alternative monitoring station AM6a was proposed and adopted for subsequent impact monitoring starting on 4th January 2016. **Table 2.1** describes the air quality monitoring locations, which are also depicted in **Figure 1**.

Table 2.1 Locations for Air Quality Monitoring

Monitoring Station	Monitored by	Location of Measurement
AM6a	DC/2009/10	Works site boundary
AM7		North West Kowloon Sewage Pumping Station
AM8		Block A of Government Dockyard

Monitoring Parameters, Frequency and Duration

- 2.3 **Table 2.2** summarizes the monitoring parameters and frequencies of impact dust monitoring for the whole construction period. The air quality monitoring schedule for the reporting period could be referred to monthly reports.

Table 2.2 Impact Dust Monitoring Parameters, Frequency and Duration

Monitoring Station	Parameter	Period	Frequency
All monitoring locations	1-hour TSP	0700-1900 hrs	3 times/ every 6 days
	24-hour TSP	0000-2400 hrs	once in every 6 days

Monitoring Methodology and QA/QC Procedure

- 2.4 The monitoring methodology and QA/QC procedures are presented in the DC/2009/10.
- 2.5 The general weather conditions (i.e. sunny, cloudy or rainy) were recorded by the field staff's observation on the monitoring day.

Results and Observations

- 2.6 All 1-hour and 24-hour TSP monitoring was conducted as scheduled in the reporting quarter. No Action/Limit Level exceedance was recorded. Summary of exceedance is presented in **Appendix B**.
- 2.7 The graphical plots of the 1-hour and 24-hour TSP monitoring results are shown in **Appendix C**.
- 2.8 According to field observations during site inspection, the identified dust sources at the monitoring stations were mainly from loading of material, vehicles movement and construction works of this Contract and other Contract in the site.

3. NOISE

Monitoring Requirements

- 3.1 Two noise monitoring stations, namely NM5 and NM6 was designated in the EM&A Manual for impact monitoring. **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.
- 3.2 Monitoring station (NM6) serves as an alternative location for FSD Diving Rescue and Diving Training Centre which is regarded as a Noise Sensitive Receiver (NSR) as it is an institution. Monitoring station (NM6), was set up at the proposed location in accordance with the Monitoring Proposal submitted by ET of Contract DC/2009/05, as agreed by the ER and IEC.

Monitoring Locations

- 3.3 Noise monitoring was conducted at two designated monitoring stations as listed in **Table 3.1**.

Table 3.1 Location of Noise Monitoring Stations

Monitoring Station	Monitored By	Location of Measurement
NM5	DC/2009/10	Near FSD Diving Rescue and Training Centre
NM6		Customs' Marine Base (Block H of Government Dockyard) Rooftop

Monitoring Parameters, Frequency and Duration

- 3.4 **Table 3.2** summarizes the monitoring parameters, frequency and total duration of monitoring. The noise monitoring schedule could be referred to monthly reports of the respective contracts.

Table 3.2 Noise Monitoring Parameters, Frequency and Duration

Monitoring Stations	Parameter	Period	Frequency
NM5 NM6	$L_{eq}(30 \text{ min.})$ dB(A)	0700-1900 hrs. on weekdays	Weekly
	$L_{eq}(5 \text{ min.})$ dB(A)	During restricted hours	Weekly Monitoring to be conducted during the construction works

Monitoring Methodology and QA/QC Procedures

- 3.5 The monitoring methodology and QA/QC procedure could be referring to Section 3 of the monthly report for Contract DC/2009/10.

Results and Observations

- 3.6 The construction noise monitoring at the designated location was conducted by the ET of Contract DC/2009/10 as scheduled in the reporting quarter. The Graphical presentation of the noise monitoring result was shown in **Appendix D**.
- 3.7 No Action/Limit Level exceedance was recorded in the reporting quarter. Summary of exceedance is presented in **Appendix B**.

- 3.8 The major noise sources identified at the designated noise monitoring stations were vehicle movement and construction equipment, as well as construction activities from this and other Contract in Stonecutters Island STW.

4. ENVIRONMENTAL AUDIT**Site Audits**

- 4.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site.
- 4.2 13 environmental site audits were conducted by ET and 3 IEC site audits were conducted for the Project in reporting quarter. No non-compliance was observed during the site audits.
- 4.3 Site inspections were undertaken to ensure and check that the implementation and maintenance of landscape and visual mitigation measures are being properly carried out in the reporting quarter in accordance to section 14.1 of the EM&A Manual. No non-compliance was observed during the site inspections.

Review of Environmental Monitoring Procedures

- 4.4 The monitoring works were conducted by the monitoring teams of Contract DC/2009/10. The monitoring procedures have been reviewed monthly.

Status of Environmental Licensing and Permitting

- 4.5 All permits/licenses obtained for the Contract DC/2009/10 are summarized in **Table 4.1**.

Table 4.1 Summary of Environmental Licensing and Permit Status

Reference Number	Valid Period		Details	Status
	From	To		
<i>Water Discharge License</i>				
WT00023103-2015	19/1/2016	31/1/2021	The application was approved on 19-1-2016.	Valid
WT00024404-2016	19/5/2016	31/5/2021	The application was approved on 19-5-2016.	Valid
WT00025973-2016	22/11/2016	31/5/2021	The application was approved on 22/11/2016.	Valid
<i>Registered Chemical Waste Producer</i>				
WPN5213-269-3584-01	N/A	N/A	The application was approved on 4-5-2011.	Valid
<i>Billing Account for Disposal of Construction Waste</i>				
CSW01444	16/3/2011	N/A	The application was approved on 16-3-2011.	Valid
<i>Notification of Works Under APCO</i>				
327427	N/A	N/A	Notice form received by EPD on 2-3-2011.	N/A
<i>Construction Noise Permit</i>				
GW-RW0536-19	10/11/2019	09/05/2020	The application was approved on 8-11-2019	Expired

Waste Management Status

- 4.6 The amount of Inert and Non Inert wastes generated by the construction activities of the Project in the reporting quarter is summarized in the waste flow table as shown in **Appendix E**.

Implementation Status of Environmental Mitigation Measures

- 4.7 Details of the implementation of mitigation measures are provided in the **Appendix G**.
- 4.8 During the weekly environmental site inspections in the reporting period, no non-conformance was identified. The observations of the site audit for the Projects are summarized in **Table 4.2a-c**.

Table 4.2a: Observations and Recommendations of Site Audits (April 2020)

Parameters	Ref. Number	Observations	Follow Up Action
Water Quality	N/A	There was no observation in the reporting period.	N/A
Air Quality	N/A	There was no observation in the reporting period.	N/A
Waste/ Chemical Management	200326-R01	General refuse should be disposed properly.	General refuse was disposed properly.
	200402-R01		
	200409-R01	Housekeeping should be improved on site.	Housekeeping was improved on site.
Landscape and Visual	N/A	There was no observation in the reporting period.	N/A
Noise	N/A	There was no observation in the reporting period.	N/A
Permit/ Licenses	N/A	There was no observation in the reporting period.	N/A

Table 4.2b: Observations and Recommendations of Site Audits (May 2020)

Parameters	Ref. Number	Observations	Follow Up Action
Water Quality	N/A	There was no observation in the reporting period.	N/A
Air Quality	N/A	There was no observation in the reporting period.	N/A
Waste/ Chemical Management	N/A	There was no observation in the reporting period.	N/A
Landscape and Visual	N/A	There was no observation in the reporting period.	N/A
Noise	N/A	There was no observation in the reporting period.	N/A
Permit/ Licenses	N/A	There was no observation in the reporting period.	N/A

Table 4.2c: Observations and Recommendations of Site Audits (June 2020)

Parameters	Ref. Number	Observations	Follow Up Action
Water Quality	N/A	There was no observation in the reporting period.	N/A
Air Quality	N/A	There was no observation in the reporting period.	N/A
Waste/ Chemical Management	200604-R01	Construction waste should be disposed of properly.	Item was remarked as 200611-R01.
	200611-R01		Construction waste was disposed of properly.
Landscape and Visual	N/A	There was no observation in the reporting period.	N/A
Noise	N/A	There was no observation in the reporting period.	N/A
Permit/ Licenses	N/A	There was no observation in the reporting period.	N/A

Implementation Status of Event Action Plans

4.9 The Event Action Plans for air quality and noise are presented in **Appendix F**.

1-hr TSP

4.10 No Action/Limit Level exceedance was recorded in the reporting quarter.

24-hr TSP

4.11 No Action/Limit Level exceedance was recorded in the reporting quarter.

Construction Noise

4.12 No Action/Limit Level exceedance was recorded in the reporting quarter.

Landscape and Visual

4.13 No non-compliance was recorded in the reporting quarter.

Summary of Complaints and Prosecutions

4.14 No environmental complaint and prosecution was received for the Project in the reporting quarter.

4.15 There were no environmental complaint and prosecution received since the commencement of the Project. The Complaint Log is presented in **Appendix H**.

5. FUTURE KEY ISSUES

Key Issues for the Coming Months

5.1 Key environmental issues in the coming months include:

- Deposal/Storage of chemicals/fuel and chemical waste/waste oil on-site;
- Stockpile should be properly covered by tarpaulin to mitigate dust generation; and
- Silt and dust getting into the public area by the leaving site vehicles at the site exits without adequate wheel washing facilities.

Construction Program for the Coming Quarter

5.2 The tentative construction program is provided in **Appendix I**.

6. CONCLUSIONS AND RECOMMENDATIONS

Conclusions

- 6.1 Environmental monitoring and audit works were performed in the reporting quarter and all monitoring results were checked and reviewed.

1-hour TSP Monitoring

- 6.2 All 1-hour TSP monitoring was conducted as scheduled in the reporting quarter. No Action/Limit Level exceedance was recorded.

24-hour TSP Monitoring

- 6.3 All 24-hour TSP monitoring was conducted as scheduled in the reporting quarter. No Action/Limit Level exceedance was recorded.

Construction Noise Monitoring

- 6.4 All construction noise monitoring was conducted as scheduled in the reporting quarter. No Action/Limit Level exceedance was recorded.

Environmental Audit

- 6.5 Environmental site audits were conducted as weekly basis in the reporting quarter. No non-compliance was recorded.

Complaint and Prosecution

- 6.6 No environmental complaint and prosecution was received in the reporting quarter.

Recommendations for the coming reporting period:

- 6.7 The following recommendations were made for the coming reporting period:

Air Quality

- To provide adequate water spray on site;
- To mitigate dust generation by adequate water spraying or covering by tarpaulin during dry days;
- To regularly maintain the machinery and vehicles on site;
- To follow up any exceedance caused by the construction works; and
- Non-Road Mobile Machinery (NRMM) labels must be demonstrated on the registered equipment for inspection.

Noise

- To inspect the noise sources inside the site;
- To follow up any exceedance caused by the construction works;
- To space out noisy equipment and position the equipment as far away as possible from

sensitive receivers;

- To provide temporary noise barriers for operations of noisy equipment near the noise sensitive receivers in an appropriate location.
- To provide adequate lubricant on mechanical equipments to reduce frictional noise; and
- To well maintain the mechanical equipments / machineries to avoid abnormal noise nuisance.

Water Quality

- To provide adequate temporary drainage system with adequate capacity;
- To provide adequate wastewater treatment facilities to treat the wastewater generated during construction works and heavy rain;
- To properly cover the stockpile and slope to prevent the generation of surface runoff; and
- To avoid water accumulation on site and carry out larviciding against mosquito breeding for stagnant water when mosquito larvae are observed.

Waste/Chemical Management

- To provide proper rubbish bins / skips for waste collection;
- To check for any accumulation of wasted materials or rubbish on site;
- To provide adequate chemical waste storage area on site;
- To avoid any discharge or accidental spillage of chemical waste or oil directly from the equipment; and
- To avoid improper handling or storage of oil drum on site.

Landscape and Visual

- To erect and maintain the protection fence around the retaining tree; and
- To avoid any heavy materials placed into tree protection zone.

FIGURES



AM7
North West Kowloon
Sewage Pumping Station

NM5
FSD Diving Rescue and
Training Centre

AM6a
Works Site Boundary

Stonecutters Island
Sewage Treatment Plant

NM6
Customs' Marine Base

AM8
Block A of
Government Dockyard

LEGEND:

DC/2009/10' SITE AREA



DC/2009/17' SITE AREA



DC/2009/18' SITE AREA



AIR QUALITY MONITORING
STATION



NOISE MONITORING STATION



Contract No: DC/2009/10
HATS 2A - Upgrading Main Pumping Station, Sedimentation Tanks and Ancillary
Facilities at SCISTW

General Location Plan of the Project and Locations of Air
Quality and Noise Monitoring Stations

SCALE

N.T.S

DATE

11/2015

CHECK

-

DRAWN

VW

JOB No.


MA11007


FIGURE NO.

1

REV

-

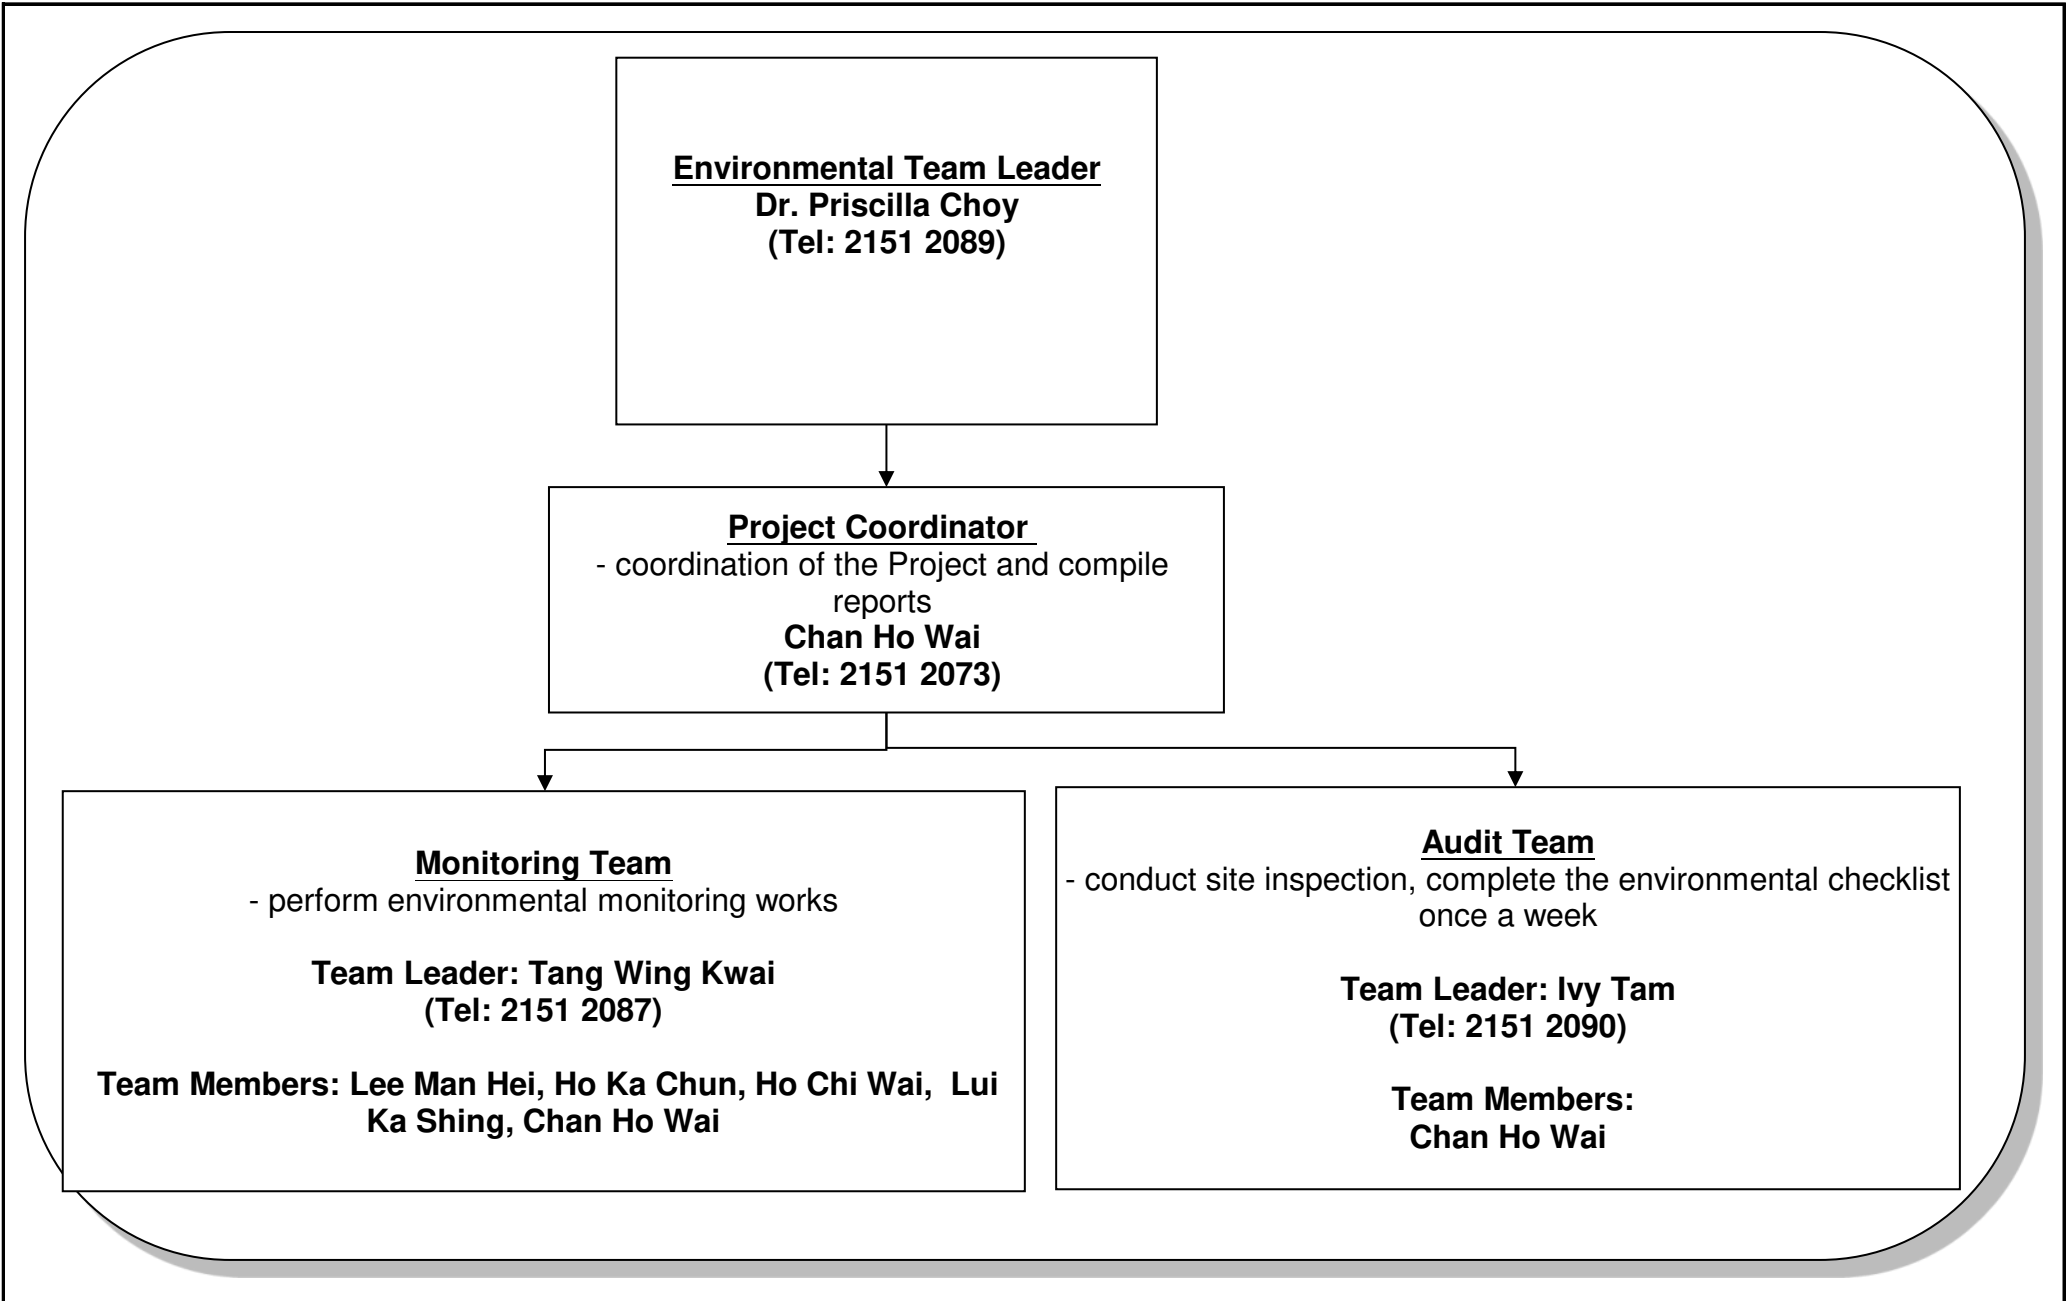

Title	Contract No. DC/2009/10 HATS Stage 2A – Upgrading Works at SISTW Main Pumping Station, Sedimentation Tanks and Ancillary Facilities ET's Organization Chart	Scale N.T.S Version v.2	Project No. MA11007 Figure 2	
-------	--	----------------------------------	---------------------------------------	---

**APPENDIX A
ACTION AND LIMIT LEVELS FOR AIR
QUALITY AND NOISE QUALITY**

Appendix A Action and Limit Levels

Table A-1 Action and Limit Levels for 1-Hour TSP and 24-Hour TSP

Monitoring Stations	Action Level ($\mu\text{g}/\text{m}^3$)		Limit Level ($\mu\text{g}/\text{m}^3$)	
	1-hour	24-hour	1-hour	24-hour
AM6a	346	196	500	260
AM7	322	207	500	260
AM8	307	158	500	260

Table A-2 Action and Limit Level for Construction Noise

Monitoring Stations	Time Period	Action Level	Limit Level in dB(A)
NM5 NM6	0700-1900 hours on normal weekdays	When one documented complaint is received	75
	Evening Time of normal weekdays and General Holidays: All days during the evening (1900 to 2300 hours), and general holidays (including Sundays) during the day-time and evening (0700 to 2300 hours)	N/A	70 ⁽¹⁾

Notes: If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

APPENDIX B
SUMMARY OF EXCEEDANCE




APPENDIX B – SUMMARY OF EXCEEDANCE

Reporting Quarterly: April to June 2020

- a) Exceedance Report for 1-hr TSP (NIL)**
- b) Exceedance Report for 24-hr TSP (NIL)**
- c) Exceedance Report for Construction Noise (NIL)**

**APPENDIX C
1-HOUR AND 24-HOUR TSP
GRAPHICAL PRESENTATION**




1-hr TSP Concentration Levels

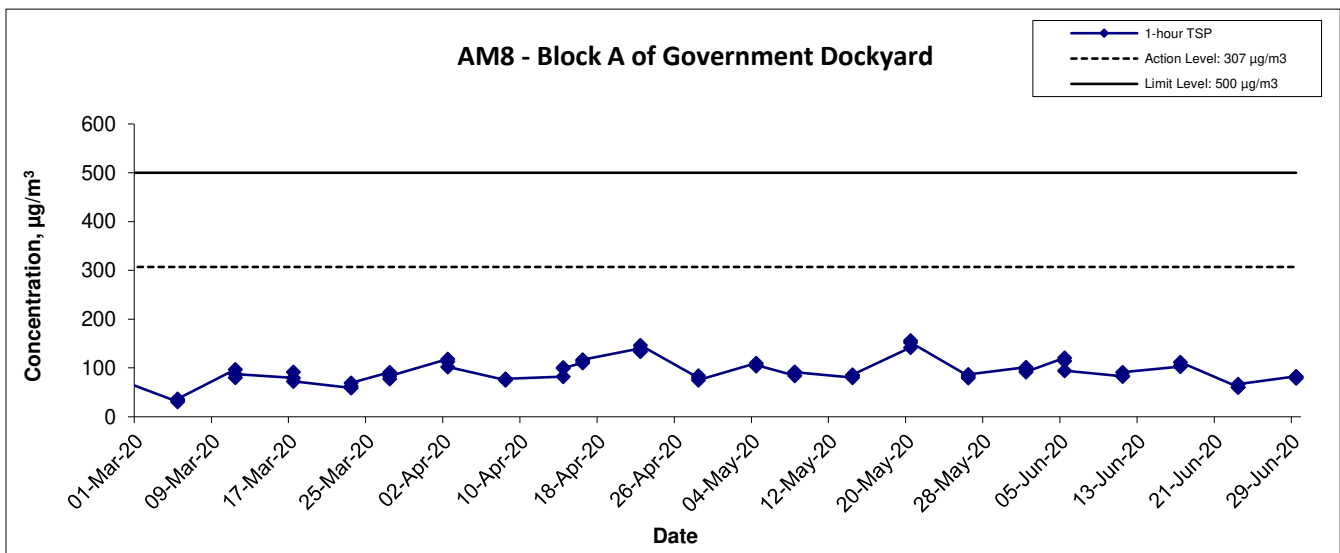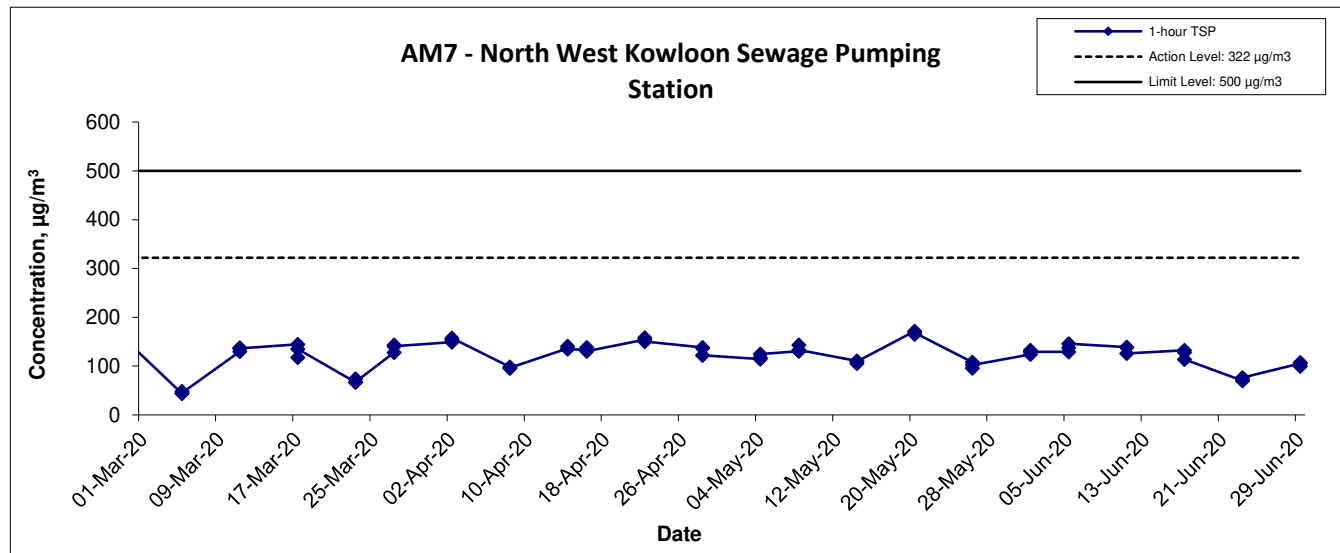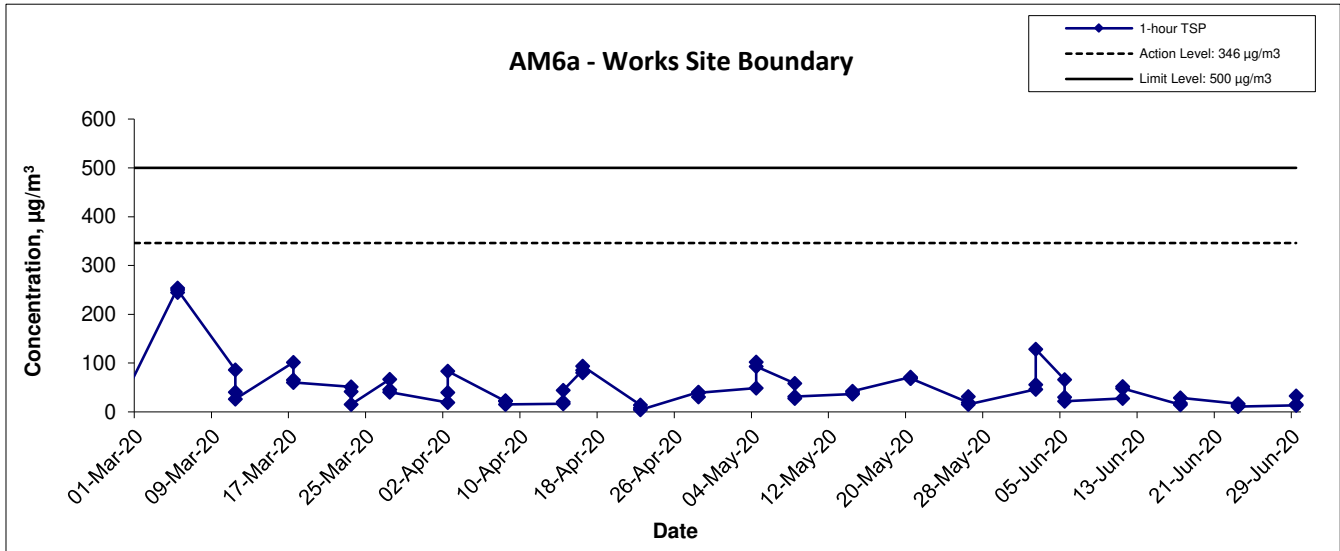

Title	Contract No. DC/2009/10		Scale	Project No. MA11007	
	HATS 2A – Upgrading Works at SCISTW– Main Pumping Station, Sedimentation Tanks and Ancillary			N.T.S	
Graphical Presentation of 1-hour TSP Monitoring Results			Date	Appendix C	
			Jun-20		



24-hr TSP Concentration Levels

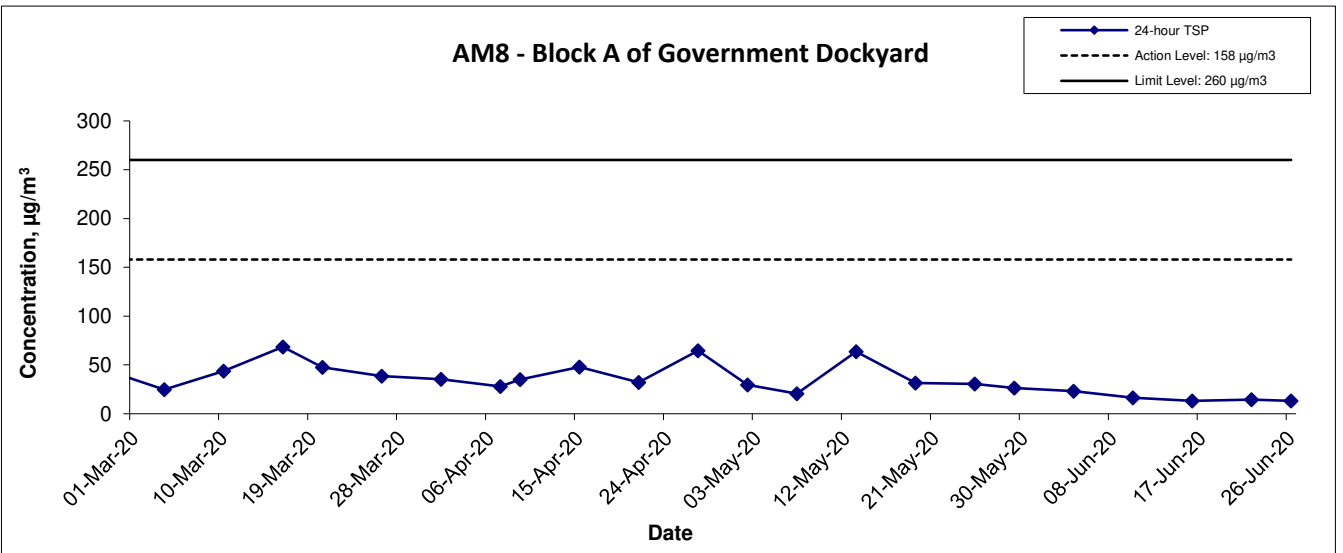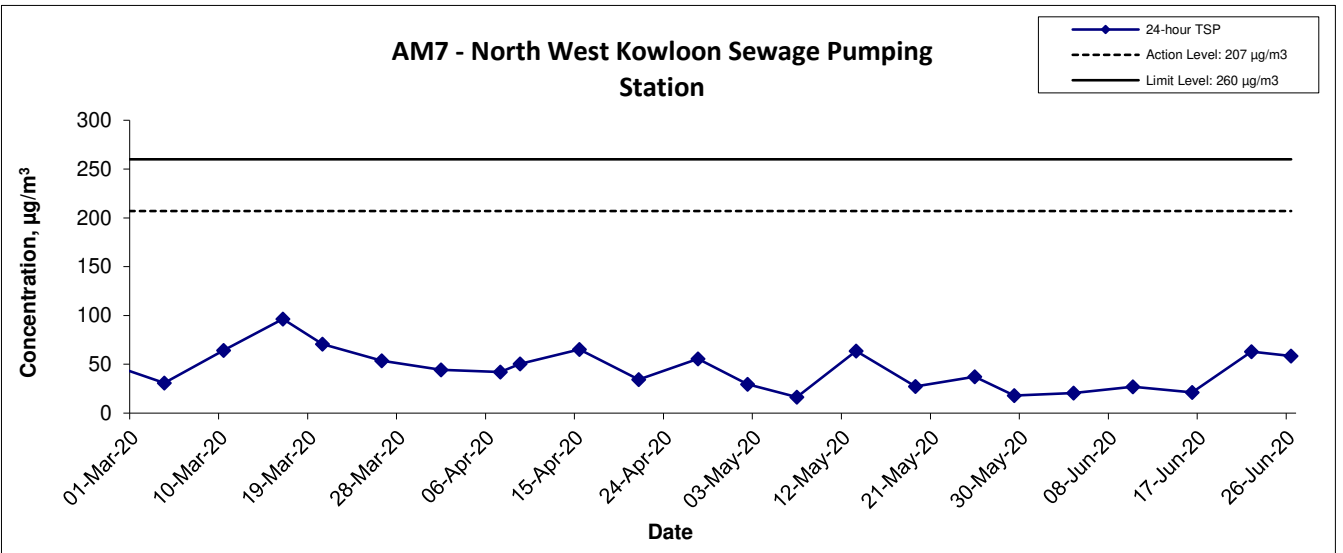
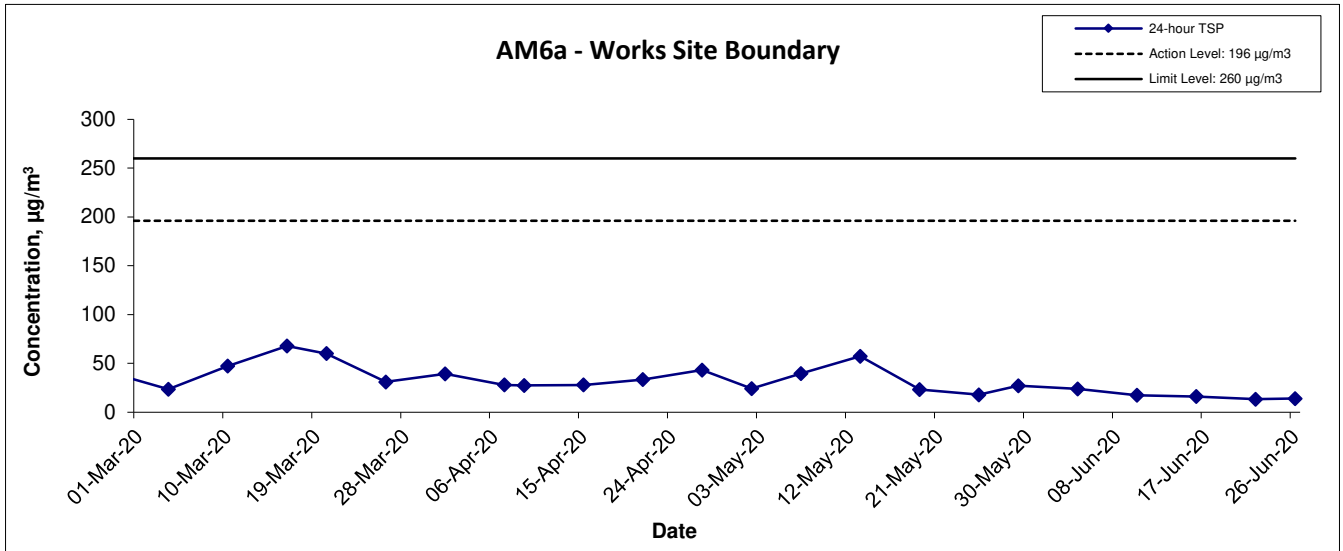


Title	Contract No. DC/2009/10	Scale	Project	
	HATS 2A – Upgrading Works at SCISTW– Main Pumping Station, Sedimentation Tanks and Ancillary	N.T.S	No. MA11007	
Graphical Presentation of 24-hour TSP Monitoring Results		Date	Appendix	
		Jun 20	C	

**APPENDIX D
NOISE MONITORING GRAPHICAL
PRESENTATIONS**

Noise Levels

(0700-1900 hrs on Normal Weekdays)

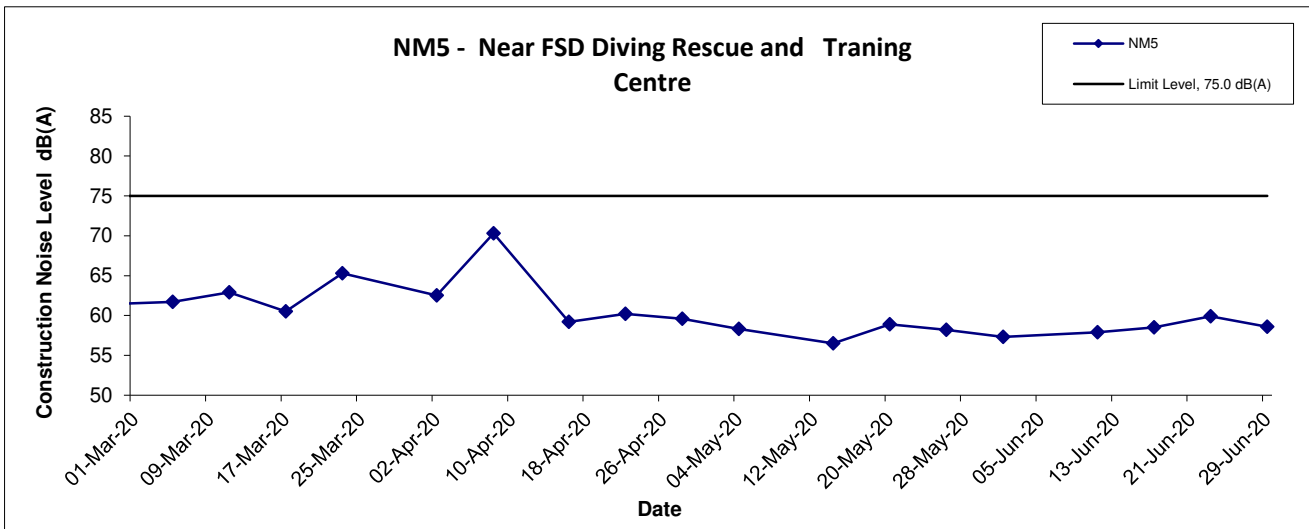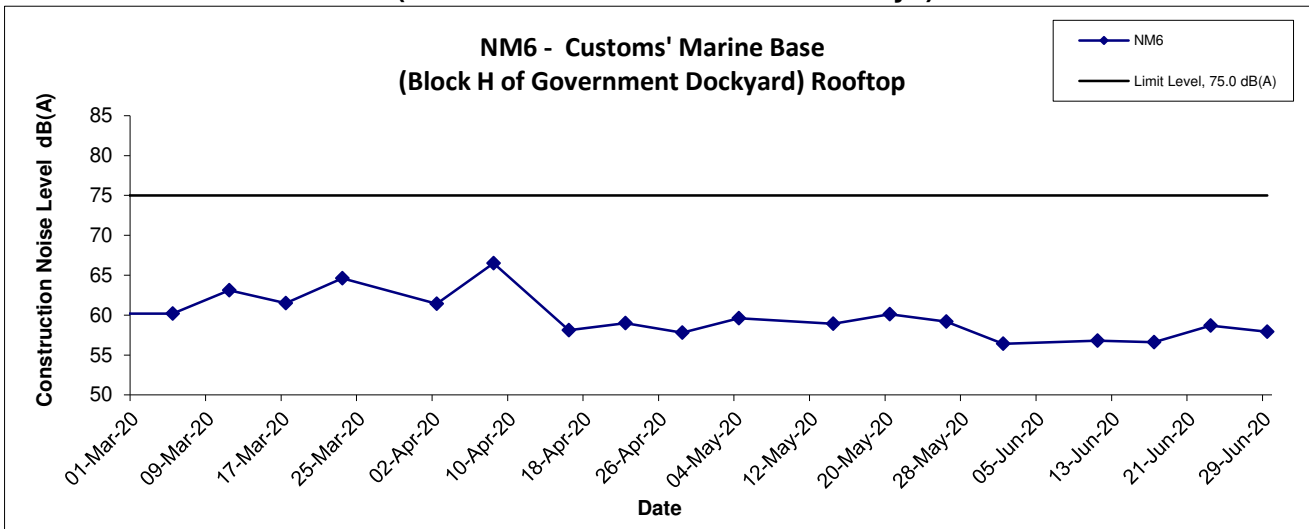

Title Contract No. DC/2009/10 HATS 2A – Upgrading Works at SCISTW– Main Pumping Station, Sedimentation Tanks and Ancillary Graphical Presentation of Noise Monitoring Result	Scale	N.T.S	Project No.	MA11007
	Date	Jun 20	Appendix	D



**APPENDIX E
SUMMARY OF AMOUNT OF WASTE
GENERATED**

Name of Department: DSD

Contract No. : DC/2009/10

Monthly Summary Waste Flow Table for 2020 (year)

Month	Actual Quantities of inert C&D Materials Generated Monthly						Actual Quantities of C&D Materials Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard	Plastics (see Note 3)	Chemical Waste	Other, e.g. general refuse
	(In '000m ³)	(In '000m ³)	(In '000m ³)	(In '000m ³)	(In '000m ³)	(In '000m ³)	(In '000kg)	(In '000kg)	(In '000kg)	(In '000kg)	(In '000m ³)
Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.005
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.002
Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.001
Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.006
May	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.003
June	0.005	0.005	0.000	0.000	0.005	0.000	0.000	0.000	0.000	0.000	0.000
Sub-total	0.005	0.005	0.000	0.000	0.005	0.000	0.000	0.000	0.000	0.000	0.018
July											
Aug											
Sep											
Oct											
Nov											
Dec											
Total	0.005	0.005	0.000	0.000	0.005	0.000	0.000	0.000	0.000	0.000	0.018
Total since commence ment of project	61.952	61.952	0.000	0.000	61.952	0.000	372.871	11.905	3.314	2.227	2.116

Notes:

- (1) The performance targets are given in PS Clause 25.41(14).
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material
- (4) The conversion factor for tonne to m³ for inert C&D materials is 1.9 tonne/m³.
- (5) The conversion factor for tonne to m³ for general refuse is 1.8 tonne/m³.

APPENDIX F
EVENT ACTION PLANS

APPENDIX F – Event / Action Plans

Table F-1 Event / Action Plan For Air Quality

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
ACTION LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET; 2. Check Contractor’s working method.	1. Notify Contractor.	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring	1. Check monitoring data submitted by ET; 2. Check Contractor’s working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
LIMIT LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
2. Exceedance for two or more consecutive samples	1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 5. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated

Table F-2 Event / Action Plan For Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	<ol style="list-style-type: none"> 1. Notify ER, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the IEC and Contractor on remedial measures required; 5. Increase monitoring frequency to check mitigation effectiveness 	<ol style="list-style-type: none"> 1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Advise the ER on the effectiveness of the proposed remedial measures 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC and ER; 2. Implement noise mitigation proposals
Limit Level being exceeded	<ol style="list-style-type: none"> 1. Inform IEC, ER, Contractor and EPD; 2. Repeat measurements to confirm findings; 3. Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contractor's working procedures; 6. Discuss with the IEC, Contractor and ER on remedial measures required; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification; 3. Implement the agreed proposals; 4. Submit further proposal if problem still not under control; 5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated

**APPENDIX G
ENVIRONMENTAL MITIGATION
IMPLEMENTATION SCHEDULE (EMIS)**

APPENDIX G IMPLEMENTATION SCHEDULE OF ENVIRONMENTAL MITIGATION MEASURES (EMIS)

EIA Ref.	Recommended Mitigation Measures	Location of the measure	Implementation Status
A	Air Quality		
3.74	Skip hoist for material transport should be totally enclosed by impervious sheeting.	All construction sites	^
	Vehicle washing facilities should be provided at every vehicle exit point.		^
	The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcore.		^
	Where a site boundary adjoins a road, streets or other areas accessible to the public, hoarding of not less than 2.4 m high from ground level should be provided along the entire length except for a site entrance or exit.		N/A
	Use of regular watering, with complete coverage, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather.		^
	Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.		^
	Open stockpiles shall be avoided or covered. Where possible, prevent placing dusty material storage piles near ASRs.		^
	Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.		^
	Imposition of speed controls for vehicles on unpaved site roads. Ten kilometers per hour is the recommended limit.		^
	Every stock of more than 20 bags of cement should be covered entirely by impervious sheeting placed in an area sheltered on the top and the 3 sides.		^
	Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites.		^
3.74	Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.	All construction sites	^

EIA Ref.	Recommended Mitigation Measures	Location of the measure	Implementation Status
B	Airborne Noise		
4.56– 4.61	Use of quiet PME, movable barriers and acoustic mats.	All construction sites	^
4.67	Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program.		^
	Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program.		^
	Mobile plant, if any, shall be sited as far away from NSRs as possible.		^
	Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum.		^
4.67	Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.		^
	Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from on-site construction activities.		^
C	Water Quality		
6.349 to 6.375	Construction Site Runoff and General Construction Activities The mitigation measures as outlined in the ProPECC PN 1/94 Construction Site Drainage should be adopted where applicable.	All construction sites	^
6.376	Effluent Discharge There is a need to apply to EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD. Minimum distances of 100 m should be maintained between the discharge points of construction site effluent and the existing saltwater intakes.		^
6.377	Accidental Spillage of Chemicals Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General)		^

EIA Ref.	Recommended Mitigation Measures	Location of the measure	Implementation Status
	Regulation should be observed and complied with for control of chemical wastes.		
6.378	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.		^
6.379	<p>Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows:</p> <ul style="list-style-type: none"> • Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport. • Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents. • Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area. 		^
6.380	<p>Construction Works in Close Proximity of Storm Drains or Seafront:</p> <p>To minimize the potential water quality impacts from the construction works located at or near any watercourse, the practices outlined below should be adopted where applicable.</p> <ul style="list-style-type: none"> • The use of less or smaller construction plants may be specified to reduce the disturbance to the storm water courses or marine environment. • Temporary storage of materials (e.g. equipment, filling materials, chemicals and fuel) and temporary stockpile of construction materials should be located well away from any water courses during carrying out of the construction works. • Stockpiling of construction materials and dusty materials should be covered and located away from any water courses. • Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby water receivers. • Construction activities, which generate large amount of wastewater, should be carried out in a distance away from the waterfront, where practicable. • Proper shoring may need to be erected in order to prevent soil/mud from slipping into the storm culvert or sea. 	All construction sites	^

EIA Ref.	Recommended Mitigation Measures	Location of the measure	Implementation Status
D	Waste Management		
9.107	Reusable steel or concrete panel shutters, fencing and hoarding and signboard should be used as a preferred alternative to items made of wood, to minimize wastage of wood. Attention should be paid to WBTC No. 19/2001 - Metallic Site Hoardings and Signboards to reduce the amount of timber used on construction sites. Metallic alternatives to timber are readily available and should be used rather than new timber. Precast concrete units should be adopted wherever feasible to minimize the use of timber formwork.	All construction sites	^
9.109	All waste materials should be segregated into categories covering: <ul style="list-style-type: none"> • excavated materials suitable for reuse on-site; • excavated materials suitable for public filling facilities; • remaining C&D waste for landfill; • chemical waste; and • general refuse for landfill. 	All construction sites	^
9.113	Sort C&D waste from demolition of existing facilities to recover recyclable portions such as metals.	All construction sites	^
	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.		^
	Encourage collection of aluminum cans, PET bottles and paper by providing separate labeled bins to enable these wastes to be segregated from other general refuse generated by the work force.		^
	Any unused chemicals or those with remaining functional capacity shall be recycled.		^
	Proper storage and site practices to minimize the potential for damage or contamination of construction materials.		*
9.115	Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	All construction sites	^
	Training of site personnel in proper waste management and chemical waste handling procedures.		^
9.115	Develop and provide toolbox talk for on-site sorting of C&D materials to enhance worker's awareness in handling, sorting, reuse and recycling of C&D materials.	All construction sites	^
	Provision of sufficient waste disposal points and regular collection of waste.		^
	Regular cleaning and maintenance programme for drainage systems, sumps and oil		^

EIA Ref.	Recommended Mitigation Measures	Location of the measure	Implementation Status
	interceptors.		
9.125	Bentonite slurries used in diaphragm wall construction should be reconditioned and reused wherever practicable. The disposal of residual used bentonite slurry should follow the good practice guidelines stated in ProPECC PN 1/94 "Construction Site Drainage".	All construction sites	^
9.131	Adequate number of portable toilets at temporary works areas or the PTWs to ensure that sewage from site staff would be properly collected.		^
9.133	General refuse should be stored in enclosed bins, skips or compaction units separating from C&D material and disposed of at designated landfill.		*
9.135	The recyclable component of the municipal waste generated by the workforce, such as aluminum cans, paper and cleansed plastic containers should be separated from other waste. Provision and collection of recycling bins for different types of recyclable waste should be set up by the Contractor. The Contractor should also be responsible for arranging recycling companies to collect these materials.		^
9.137	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a chemical waste producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the approved Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.		^
9.142	Prior to excavation of the marine deposit layer, the deposit should be tested in accordance with the ETWB TC(W) No. 34/2002 and the results should be presented in a Preliminary Sediment Quality Report. The marine deposit should be disposed of at the disposal site designated by the Marine Fill Committee (MFC) or Director of Environmental Protection (DEP) depending on the test results.		N/A

EIA Ref.	Recommended Mitigation Measures	Location of the measure	Implementation Status
E	Terrestrial Ecology		
10.94	To implement effective noise mitigation measures as recommended in Section 4 of EIA.	All construction sites	N/A
10.95	Dust control practices such as regular watering, complete coverage of any aggregate or dusty material storage piles, and re-schedule of dusty activities during high-wind conditions as well as other measures recommended in Section 3 of EIA, should be implemented.		^
10.96	Fences/hoardings should be erected and installed along the boundary of the works areas.		^
10.97	Standard good site practices as suggested in Section 10 of EIA should be implemented.		N/A
10.98	Provision of proper drainage system and runoff control measures such as use of sand/silt traps, oil/grease separators, sedimentation tanks, etc.		^
F	Landscape and Visual		
Table 13.7	Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where practical.	All construction sites	^
	Existing trees to be retained on site should be carefully protected during construction.		^
	Trees unavoidably affected by the works should be transplanted where practical.		^
	Compensatory tree planting should be provided to compensate for felled trees.		^
	Control of night-time lighting.		^
Table 13.7	Erection of decorative screen hoarding compatible with the surrounding setting.	All construction sites	N/A
G	Marine Ecology		
11.137	To minimize the potential indirect impacts on water quality from construction site runoff and various construction activities, the practices outlined in ProPECC PN 1/94 Construction Site Drainage should be adopted.	All construction sites	^
H	Hazard to Life		
14A.201	Limiting use of cranes in terms of locations, lifting height, swing angle and setting up safety zone.	Exact location will be determined on construction site by the engineer	^

Remarks:	^ Compliance of mitigation measure;
	N/A Not Applicable;
	* Recommendation was made during site audit but improved/rectified by the contractor.
	# Recommendation was made during site audit and to be improved / rectified by the contractor.
	X Non-compliance of mitigation measure;
	• Non-compliance but rectified by the contractor;

**APPENDIX H
COMPLAINT LOG**

APPENDIX H – COMPLAINT LOG**Reporting Quarter:** April to June 2020

Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
N.A.	N.A.	N.A.	N.A.	N.A.	N.A.

Remarks: No environmental complaint was received in the reporting quarter.

APPENDIX I
CONSTRUCTION PROGRAMME

Activity ID	Activity Name	Activity % Complete	Original Duration	Start	Finish	2020		2021
						Q3	Q4	Q1
Target Works Programme (Completion for Section 3, 4 and 5)								
Works for Section 3								
MPS2								
F.S system (Office level, FS pump room)								
A9620	FSD Inspection (including FS, MVAC and Hot smoke test)	90%	210	27-Mar-19 A	26-Aug-20			23-Jan-21, Target Works Programme (Completion for Section 3, 4 and 5)
Sodium Hypochlorite Storage Compound								
C3 and C4 dosing pipes								
A8720	DCS upgrading at Daytanks	5%	120	02-Nov-19 A	15-Dec-20			23-Jan-21, Sodium Hypochlorite Storage Compound
Documentation								
A3601	Training to ST2	10%	18	28-Mar-20 A	07-Jan-21			23-Jan-21, Documentation
A3602	Handover inspection of NaOCl Daytank DSD/ST2 (Stage three)	0%	14	07-Jan-21	23-Jan-21			Handover inspection of NaOCl Daytank DSD/ST2 (Stage three)
A3605	Handover of NaOCl Daytank (stage three)	0%	0		23-Jan-21			Handover of NaOCl Daytank (stage three)
Supplementary Agreement No.2								
MPS2 Pump Upgrading (2nd Stage)								
A9262	Installation and testing of upgraded pumps (4Nos)	10%	120	02-Sep-19 A	16-Nov-20			16-Dec-20, MPS2 Pump Upgrading (2nd Stage)
A9272	Submit performance report, O&M manual for upgrading works	0%	30	17-Nov-20	16-Dec-20			16-Dec-20, Supplementary Agreement No.2
DOU3 upsizing								
A9790	Preparaton works for FPR vessel dismantling, including Mod of pipelines, air ducts and scaffolds	0%	24	01-Aug-20	24-Aug-20			10-Nov-20, DOU3 upsizing
A9800	Discommissioning and replacement of new FRP vessels	0%	14	11-Aug-20	24-Aug-20			
A9810	Replacement of recirculation pumps, nutrient pumps and associated pipeworks	0%	12	25-Aug-20	05-Sep-20			
A9820	Installation of instruments	0%	12	25-Aug-20	05-Sep-20			
A9830	Testing and commissioning	0%	10	06-Sep-20	15-Sep-20			
A9840	Final testing and commissioning (including air balancing and performance test)	0%	16	16-Sep-20	01-Oct-20			
A9850	Reliability test of upgraded DOU	0%	30	02-Oct-20	31-Oct-20			
A9860	As-built drawings and OM manual submission and defect rectification	0%	25	02-Oct-20	26-Oct-20			
A9870	Provide Operational Training to ST2	0%	5	01-Nov-20	05-Nov-20			
A9880	Handover to ST2	0%	5	06-Nov-20	10-Nov-20			

█ Actual Work ◆ Milestone
█ Remaining Work ◀ Summary
█ Critical Remaining Work

Contract No. DC/2009/10
HATS Stage 2A - Upgrading works at StoneCutters Island Sewage Treatment Works
 Target Works Programme for Completion of Section 3, 4 and 5

Sheet 1 of 1	Date	Revision	Checked	Approved
	26-Jul-18	Rev. 5		
	20-Nov-18	Rev. 6		
	11-Feb-19	Rev. 7		
