


Highways Department


**Contract No.
HY/2007/14 Widening of
Tuen Mun Road at
Tsing Tin Interchange**

Monthly Environmental
Monitoring and Audit
Report - May 2009

Revision 2



Certified by Environmental Team Leader
Coleman Ng
Ove Arup & Partners Hong Kong Ltd



Verified by Independent Environmental Checker
Antony Wong
Hyder Consulting Limited

* Subject to exclusion of noise monitoring results
and bi-annual calibration for both sound level meter
(B&K Type 2238) and acoustic calibrator (B&K Type 1
4231) which contradicts the verified Baseline
Monitoring Report dated Sep 2008 for this project
and manufacturer's recommendation of annual
calibration.

Contents

	Page
Executive Summary	1
1 Environmental Status	3
1.1 Construction Programme	3
1.2 Work Undertaken During the Month	3
1.3 Project Area, Sensitive Receivers and Environmental Monitoring Locations	4
Status of	6
1.4 Environmental Licensing and Permitting	6
2 Implementation Status	7
3 Air Monitoring	8
3.1 Air Monitoring Requirements	8
3.2 Air Monitoring Methodology	8
3.3 Monitoring Results and Observations	10
4 Noise Monitoring	11
4.1 Noise Monitoring Requirements	11
4.2 Noise Monitoring Methodology	11
4.3 Monitoring Results and Observations	12
5 Landscape and Visual Monitoring	14
5.1 Landscape and Visual Impact Monitoring Requirements	14
5.2 Audit Results	14
5.3 Implementation Status of Consultation Phase Landscape and Visual Mitigation Measures	17
5.4 Recommendations, Corrective Actions and Outstanding Issues	17
6 Waste Disposal	18
7 Environmental Performance	19
7.1 Environmental Site Inspection	19
7.2 Non-Compliance Record	19
7.3 Complaint Record	19
7.4 Notification of Summons and Successful Prosecution	19
7.5 Review of Reasons of Non-Compliance	19
8 Future Key Issues	20
8.1 Key Issues for the Coming Month	20
8.2 Solid and Liquid Waste Management Status	20
8.3 Effectiveness and Efficiency of Mitigation Measures	20
8.4 Environmental Monitoring Program for the Forth-coming Month	20
9 Conclusions and Recommendations	21
9.1 Conclusions	21

9.2	Recommendations	21
10	Reference	21

Figures

Figure 1-1	Locations of the major construction activities
Figure 1-2	Site location plan
Figure 1-3	Location of environmental sensitive receivers and monitoring stations

Tables

Table 1-1	Major construction activities in May 2009
Table 1-2	Contacts of key environmental staff
Table 1-3	Summary of impact air quality and noise monitoring stations
Table 1-4	Summary of environmental licensing and permit status
Table 3-1	TSP monitoring parameters and frequency
Table 3-2	Action and Limit Levels for air quality
Table 3-3	Air quality equipment list for the air quality monitoring
Table 3-4	Summary of impact air quality monitoring results for May 2009
Table 4-1	Construction noise Monitoring parameters and frequency
Table 4-2	Action and Limit levels for construction noise
Table 4-3	Noise equipment list for noise monitoring
Table 4-4	Summary of impact noise monitoring in the reporting month
Table 5-1	Status of tree transplantation
Table 5-2	Status of forty trees to be affected during the construction stage
Table 6-1	Estimated amounts of waste generated in reporting month
Table 6-2	Actual amounts of waste generated in previous month (April 2009)
Table 7-1	Key findings of weekly environmental site audit in the reporting month
Table 8-1	Tentative programme of construction works

Appendices

Appendix A

Construction Programme

Appendix B

Calibration Spreadsheets of the High Volume Samplers and Calibration Certificate of Calibration Kit

Appendix C

Impact Air Monitoring Results

Appendix D

Wind Data

Appendix E

Calibration Certificate of Sound Level Meter and Acoustical Calibrator

Appendix F

Impact Noise Monitoring Results

Appendix G

Locations of the Transplanted Tress

Appendix H

Updated Summary of Environmental Mitigation Implementation Schedule

Appendix I

Monthly Summary Waste Flow Table

Appendix J

Environmental Monitoring Programme for Coming Months

Executive Summary

This is the eighth monthly Environmental Monitoring and Audit (EM&A) report prepared by Ove Arup & Partners Hong Kong Limited (Arup), the designated Environmental Team (ET), for the Project "Widening of Tuen Mun Road at Tsing Tin Interchange". This report presents the results of EM&A works conducted in the month of May 2009.

In the reporting month, the following activities took place for the Project:

- Site clearance;
- Re-compaction of fill slope;
- Existing Underground Utilities (UU) lowering;
- Construction of pile cap;
- Construction of noise barrier footing; and
- Road pavement and drainage for widen lane.

Monitoring of 1-hour and 24-hour Total Suspended Particulates (TSP) and noise during non-restricted hours was performed and the results were checked and reviewed. Site audits were conducted on weekly basis. The implementation of the environmental mitigation measures, Event and Action Plans and environmental complaint handling procedures were checked.

Impact monitoring was carried out at three sensitive receivers including AM1(a), AM3(a) and TLLF(a) during the reporting month.

Environmental Monitoring Works – Breaches of Action and Limit Levels

Air Quality

All measured 1-hour and 24-hour TSP concentrations in the reporting month were below the Action and Limit (AL) Levels.

Noise

Two (2) limit level exceedance for noise measurement during non-restricted hours were recorded on 18 and 29 May 2009. Based on field observations, it was revealed that the exceedances were mainly caused by traffic vehicles along Tuen Mun Road. It was therefore concluded that the noise exceedance was not related to the construction activities. No further actions were considered to be required. No night works were carried out during the reporting month.

Landscape and Visual Audit

In accordance with the Clause 2.7 of the EP, seven numbers of trees within the site shall be transplanted to their designed transplanted locations prior to the operational phase of the Project.

Four (tree no. 1, 16, 35 and 169) out of the seven trees were fell prior to the commencement of the construction due to typhoon and tree no. 63 was dead after transplanting in March 2009. Interim transplanting of one tree (tree no. 411) was completed and one tree (tree no. 69) was relocated to new transplanting location in April 2009.

In accordance with Tree Assessment Schedule in Appendix 10.1 of the EIA Report, forty-seven trees of LR1 and LR2, including the seven trees mentioned above, would be affected as a result of the construction works. In the reporting period, these forty trees have been removed. Twenty-eight of them were already felled. In order to minimize the quantities of felled trees, the remaining twelve trees were transplanted to Siu Lang Shui Road as agreed by LCSD and ER. No significant change on their status was noted during the reporting period.

Thirty-five numbers of trees, which shall be retained in the site according to the Tree Assessment Schedule in Appendix 10.1 of the EIA Report, were damaged due to the typhoons prior to the commencement of the construction.

The design, implementation and maintenance of landscape and mitigation measures, listed in Table 8.2 of the EM&A manual, were checked during the monthly site audit. No non-compliance has been triggered. .

Waste Disposal

Inert C&D materials with estimated amount of 820 m³ were generated in the reporting month and were disposed of at public fill. It was advised from the Contractor that determination of the actual amount of waste generation is still in progress so the relevant information will be presented on the next EM&A report.

Environmental Licensing and Permitting

Permits or licenses granted to the Project included the Environmental Permit of the Project (EP-302/2008/B), Discharge License under WPCO (EP760/425/013454/I), Construction Noise Permit under NCO (GW-RW0044-09), Chemical Waste Producer Registration under WDO (WPN5111-425-C1186-09).

Environmental Auditing

A total of 4 environmental site audits were conducted on a weekly basis in May 2009. No non-conformance to the environmental requirements was identified during the reporting period.

Complaint Log

No complaints in relation to the environmental issues was made against the Project in the reporting period.

Notifications of Summons and Successful Prosecutions

No summonses or prosecutions related to the environmental issues was made against the Project in the reporting period.

Reporting Changes

There were no reporting changes in the reporting month.

Future Key Issues

Key environmental issues to be considered in the forth-coming month include dust generation from activities on-site, noise impact from operating equipment and night works activities, uncontrolled water discharge into nearby water body, storage and using of chemicals/fuel and chemical waste/waste oil on site, disposal of construction waste and tree maintenance. Attention shall be paid to environmental issues identified in EIA report and weekly site audit. Mitigation measures recommended in EIA report and Mitigation Measure Implementation Schedule shall be fully implemented.

1 Environmental Status

1.1 Construction Programme

An up-to-date 3-month rolling construction programme to July 2009 is attached in **Appendix A**.

The construction activities were carried out together with all necessary mitigation measures stipulated in the EIA report.

1.2 Work Undertaken During the Month

The major construction activities carried out by the Contractor in the reporting month are summarised in **Table 1-1**. Locations of the construction activities are illustrated in **Figure 1-1**. Contacts of key environmental staff of the Project are shown in **Table 1-2**.

Table 1-1 Major construction activities in May 2009

Construction Activities	Location	Daily Excavation Rate
Site clearance	Whole Site Area	Range: 0 to 32 m ³
Construction of noise barriers footing	Whole Site Area	
Construction of sign gantry footing	Whole Site Area	
Road pavement and drainage for widen lane	Whole Site Area	
Drainage & road re-construction	Whole Site Area	
Re-compaction of fill slope	Whole Site Area	Not applicable

Figure 1-1 Locations of the major construction activities

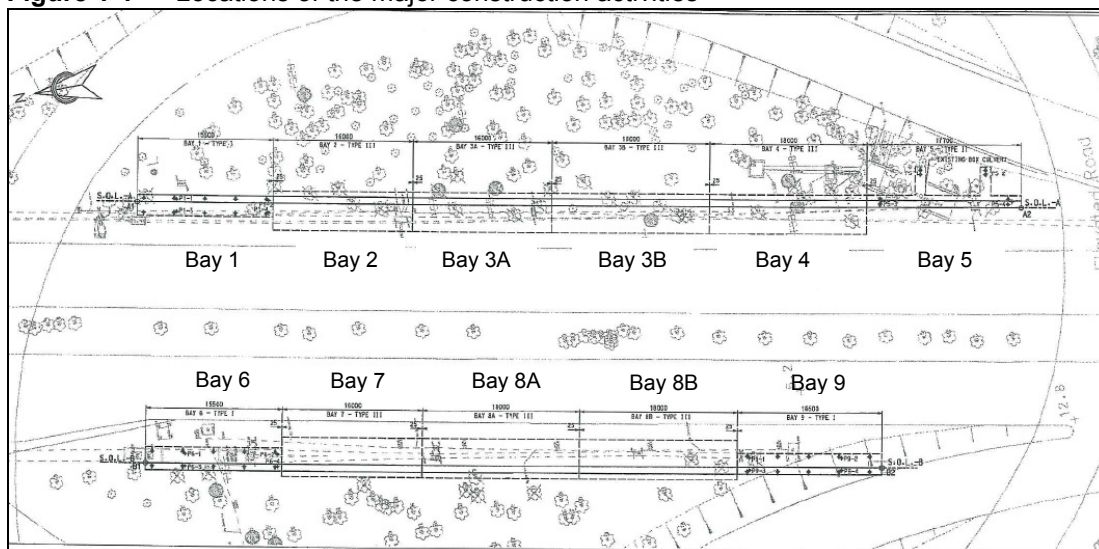


Table 1-2 Contacts of key environmental staff

Organization	Name	Telephone
Environmental Protection Department		
Environmental Protection Officer (Strategic Assessment) ²²	Thomas To	2835 1103
Engineer's Representative		
Highways Department		
Senior Engineer	K.C. Lai	2762 4951
Independent Environmental Checker		
Hyder Consulting Ltd		
Senior Environmental Consultant	Antony Wong	2911 2744
Environmental Team		
Ove Arup & Partners Hong Kong Ltd		
Environmental Team Leader	Coleman Ng	2268 3097
Contractor		
China Harbour Engineering Company Limited		
Project Manager	Eric Wu	9786 8630
Site Agent	Gordon Ng	9203 7503
Project Engineer	Jeffery Wong	6070 0143
Safety and Environmental Officer	Brian Cheung	5168 7867
Environmental Supervisor	W.P. Wong	9876 2132

1.3 Project Area, Sensitive Receivers and Environmental Monitoring Locations

The project area and the location of the sensitive receivers and monitoring stations are shown in **Figures 1-2 and 1-3** respectively, while **Table 1-3** shows the detail correspondences of monitoring stations.

Figure 1-2 Site location plan

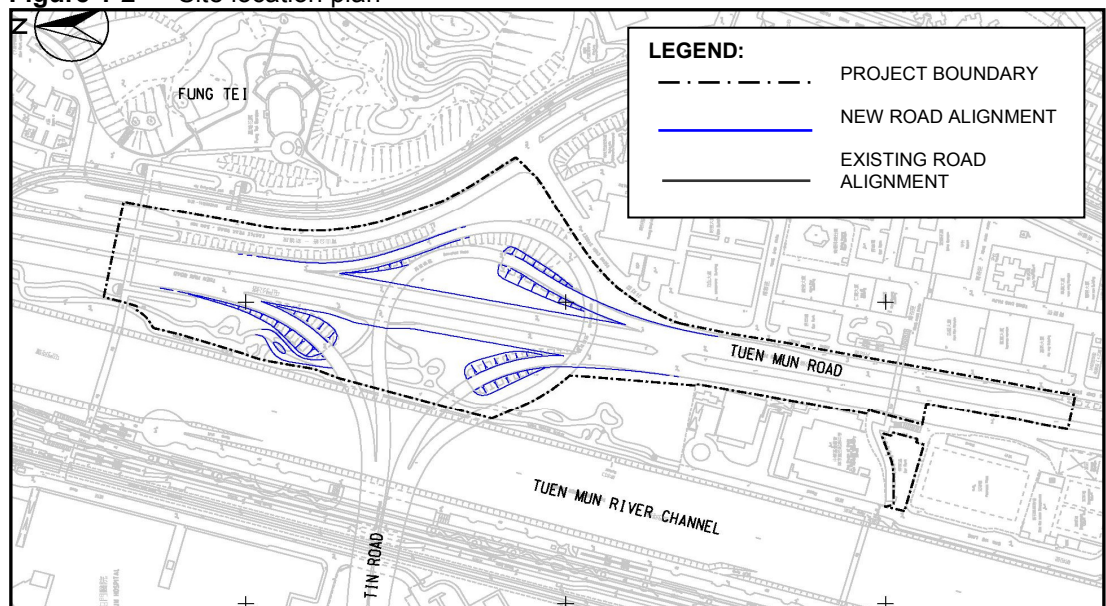


Figure 1-3 Location of environmental sensitive receivers and monitoring stations

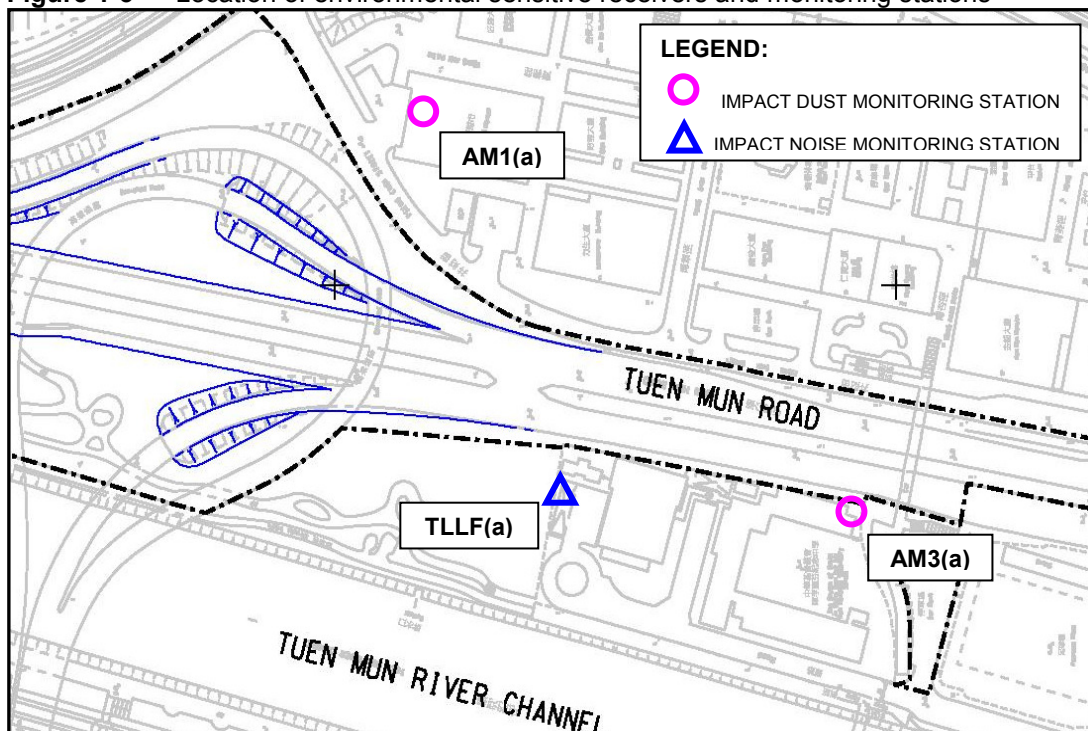


Table 1-3 Summary of impact air quality and noise monitoring stations

ID	Premise	Address	Monitoring Location Detail
Air			
AM1(a)	Kwong Choi Market	2 Tsing Min Path	Roof-top of the market office at the market garden
AM3(a)	The Church of Christ in China Tam Lee Lai Fun Memorial Secondary School	10 San Wo Lane	Ground-floor garden at the corner of the school
Noise			
TLLF(a)	The Church of Christ in China Tam Lee Lai Fun Memorial Secondary School	10 San Wo Lane	Car park of the school, facing to the construction area.

1.4 Status of Environmental Licensing and Permitting

All permits/licences inspected in the reporting month are summarised in **Table 1-4**. They are all properly kept by the contractor at their site office.

Table 1-4 Summary of environmental licensing and permit status

Types of Permits / Licenses	Reference No.	Valid from	Valid to
Environmental Permit	EP-302/2008 EP-302/2008/A EP-302/2008/B	19 February 2008 25 March 2008 15 April 2009	Superseded Superseded N/A
Notification of Construction Work under APCO	001031161	N/A	N/A
Discharge Licence under WPCO	EP760/425/013454/I	1 August 2008	31 August 2013
Construction Noise Permit	GW-RW0044-09	20 February 2009	19 August 2009
Chemical Waste Producer Registration	WPN5111-425-C1186-09	17 July 2008	N/A
Billing account for disposal of construction waste	7007413	N/A	N/A

2 Implementation Status

During weekly site inspections, the environmental protection, and pollution control/mitigation measures in accordance with the requirements stipulated in the EIA report were observed. Here below summarises the key observations and ET's corresponding recommendations while the Contractor's response and follow-up status are described in Section 7.1.

Water Quality Mitigation Measures

- Washing of site exit was observed outward to the road. The Contractor was reminded to spray inward to the site.

Waste / Chemical Waste Management

- Housekeeping at the South Bound of the site should be improved. The Contractor was reminded to clean the u-channel in routine practice.

3 Air Monitoring

3.1 Air Monitoring Requirements

Monitoring Parameters

Air quality monitoring shall be measured in terms of the TSP levels for both 24-hour and 1-hour periods.

Monitoring Frequency

Dust monitoring was carried out during the reporting month. The monitoring parameters and frequency are summarised in **Table 3-1**.

Table 3-1 TSP monitoring parameters and frequency

Parameters	Monitoring Frequency	Time Period	No. of Measurement at each Location
24-hour TSP	Once every six days	0000 – 2400	1
1-hour TSP	Three times every six days	0700 – 1900	1

Monitoring Locations

In accordance with the EM&A Manual and the subsequent Baseline Report, two air quality monitoring locations during construction stage are required, namely:

- (i) Kwong Choi Market at 2 Tsing Min Path (AM1(a)); and
- (ii) The Church of Christ in China Tam Lee Lai Fun Memorial Secondary School at 10 San Wo Lane (AM3(a)).

Wind Monitoring

Wind monitoring data including wind speed and wind directions shall be collected from Hong Kong Observatory – Tuen Mun Wind Monitoring Station.

Environmental Quality Performance Limits

The monitoring results will be checked against the Action and Limit levels described in the Baseline Report, of which they are excerpted and summarised in **Tables 3-2**.

Table 3-2 Action and Limit levels for air quality

Level	Air Monitoring Stations			
	AM1(a)		AM3(a)	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
Action Level, $\mu\text{g}/\text{m}^3$	323	161	305	168
Limit Level, $\mu\text{g}/\text{m}^3$	500	260	500	260

3.2 Air Monitoring Methodology

3.2.1 Monitoring Equipment

High Volume Sampler (HVS) was used to monitor the 24-hour and 1-hour TSP. **Table 3-3** shows the equipment used for the air quality monitoring.

Table 3-3 Air quality equipment list for the air quality monitoring

Equipment	Manufacturer & Model No	Measurement Parameter	Quantity
High Volume Sampler	GS-2310105 & TE-5170	1- hour and 24-hour TSP	2
Fibreglass Filter	G810		42
HVS Calibration Kit	GMW-2535		1

3.2.2 Maintenance and Calibration

The HVSs and their accessories were frequently checked and maintained in accordance with the manufacturer's operation and maintenance manual. The maintenance included checking of supporting screen and gasket, as well as routine replacement of motor carbon brushes for the blower motor. The power cords and power supply were checked each time before sampling to ensure proper operation.

The HVSs were calibrated at 2-month intervals using GMW-2535 calibration kit which is re-calibrated by the manufacturer after one year of use. The calibration spreadsheets of the HVS and calibration certificate of the calibration kit are provided in **Appendix B**.

3.2.3 Monitoring Procedures

Specifications of the HVS are as follows:

- 0.6 – 1.7 m³/min (20 – 60SCFM);
- Equipped with a timing/control device with +/- 5 minutes accuracy for 24 hours operation;
- Installed with elapsed time meter with +/- 2 minutes accuracy for 24 hours operation;
- Capable of providing a minimum exposed area of 406 cm² (63in²);
- Flow control accuracy: +/-2.5% deviation over 24-hr sampling period;
- Equipped with a shelter to protect the filter and sampler;
- Incorporated with an electronic mass flow rate controller or other equivalent devices;
- Equipped with a flow recorder for continuous monitoring;
- Provided with a peaked roof inlet;
- Incorporated with a manometer;
- Able to hold and seal the filter paper to the sampler housing at horizontal position;
- Easy to change the filter; and
- Capable of operating continuously for 24-hour period.

The HVSs were equipped with an electronic mass flow controller and calibrated against a traceable standard at regular intervals. All equipment, calibration kit and filter papers were clearly labelled.

The relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and other special phenomena observed and work progress of the concerned site were recorded.

A HOKLAS accredited laboratory (ALS Technichem (HK) Pty Ltd (HOKLAS no.: 066)), in accordance with their standard QA/QC procedures, with constant temperature and humidity control as well as equipped with necessary measuring and conditioning instruments to handle the 1-hour and 24-hour TSP samples was employed for sample analysis, and equipment calibration and maintenance. Filter papers of size 8"x10" were labelled before sampling. They were inspected clean with no pin holes and conditioned in a humidity controlled chamber for over 24-hr and be pre-weighed before use for the sampling.

After 1-hour and 24-hour sampling, the filter papers loaded with dust were kept in a clean and tightly sealed plastic bag, and then returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. All the collected samples were kept in a good condition for 6 months before disposal.

3.3 Monitoring Results and Observations

3.3.1 Weather Condition

No adverse weather conditions, in particular adverse wind speed & wind direction and fog & rain that may significantly affect or invalidate the collected monitoring data, were registered during the reporting period.

3.3.2 Air Quality Monitoring Results

Monitoring of 1-hour TSP was conducted at all monitoring stations on 6, 12, 18, 23 and 29 May 2009, while monitoring of 24-hour TSP was conducted on 4, 7, 13, 19, 25 and 30 May 2009. All monitoring data and graphical presentation of the monitoring results are provided in **Appendix C** and are summarised in **Table 3-4**. The graphical presentation of the monitoring results over past four months (February to May 2009) are provided in **Appendix C**. Wind data during the reporting period is presented in **Appendix D**.

Table 3-4: Summary of impact air quality monitoring results for May 2009

Location	Average 1-hr TSP Concentration, $\mu\text{g}/\text{m}^3$ (Range)	Average 24-hr TSP Concentration, $\mu\text{g}/\text{m}^3$ (Range)
AM1(a)	12 (7 – 14)	44 (26 – 64)
AM3(a)	30 (7 – 175)	33 (6 – 55)

All measured 1-hour and 24-hour TSP concentrations in the reporting month were below the Action/Limit Level. No exceedance of action and limit level was found.

3.3.3 General Observations

Major construction works including sheet pile installation for noise barrier footing, excavation for noise barrier footing and UU slewing, fill slope re-compaction and noise barriers footing construction were implemented during the reporting month.

Observable dust generation from activities on-site, such as vehicular movements along unpaved area, excavation and demolition, had been noticed at the monitoring location during the air monitoring period.

4 Noise Monitoring

4.1 Noise Monitoring Requirements

Monitoring Parameters

Construction noise shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). L_{10} and L_{90} shall also be recorded as supplementary reference information for data auditing.

Monitoring Frequency

Noise measurements shall be conducted on a weekly basis. The monitoring time periods, monitoring parameters and frequency are summarised in **Table 4-1**.

Table 4-1 Construction noise monitoring parameters and frequency

Time Period (when construction activity is found)	Parameters	Monitoring Frequency	No. of Measurement at each Location
Between 0700-1900 hours on normal weekdays	$L_{eq}(30 \text{ min})$	Once per week	1
Between 1900-2300 hours on normal weekdays	$L_{eq}(5 \text{ min})^*$		3 (consecutive)*
Between 2300-0700 hours of next day			
Between 0700-1900 hours on holidays			

* If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

Monitoring Location

In accordance with the EM&A Manual and the subsequent Baseline Report, one noise monitoring location during construction stage is required, namely:

- (i) The Church of Christ in China Tam Lee Lai Fun Memorial School at 10 San Wo Lane (TLLF(a)).

Environmental Quality Performance Limits

The monitoring results will be checked against the Action and Limit levels described in the Baseline Report, of which they are excerpted and summarised in **Tables 4-2**.

Table 4-2 Action and Limit levels for construction noise

Time Period	Action Level	Limit Level dB(A)
0700 - 1900 hours on normal weekdays	When one documented complaint is received	70 / 65 (Note 1)
0700 - 2300 hours on holiday; and 1900 – 2300 hours on all other days		70 (Note 2)
2300 – 0700 hours of next day		55 (Note 2)

Notes:

1. For normal day-time working hours, the noise criteria are 70 dB(A) and 65 dB(A) for normal reaching periods and examination period respectively.
2. If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

4.2 Noise Monitoring Methodology

4.2.1 Monitoring Equipments

Noise level was measured by a Sound Level Meter (SLM) in terms of A-weighted equivalent continuous sound pressure level. L_{eq} , L_{10} and L_{90} were recorded as supplementary information for data auditing. **Table 4-3** shows the equipment list of the noise monitoring.

Table 4-3 Noise equipment list for noise monitoring

Equipment	Manufacturer & Model No.	Serial no.	Precision Grade	Qty.
Integrated SLM	Brüel & Kjær 2238	2562763	IEC 651 Type 1	1
½" free-field microphone	Brüel & Kjær 4188	2658599	IEC 804 Type 1	1
Windshield	Brüel & Kjær UA0237	N/A		1
Acoustical calibrator	Brüel & Kjær 4231	2314016	IEC 942 Type 1	1

4.2.2 Maintenance and Calibration

The SLM and calibrator in compliance with the International Electrotechnical Commission (IEC) Publication 651:1979 (Type 1) specifications as referenced in the Technical Memorandum on Noise from Construction Work other than Percussive Piling (GW-TM) was used. The calibration certificates for the noise equipments are provided in **Appendix E**.

SLM complying with the standards of IEC 651 (Fast, Slow, Impulse rms detector tests) and IEC 804 (L_{eq} functions) and acoustical calibrator model no. 4231 complying with IEC 942 were adopted for the noise measurement. The SLM is calibrated by its manufacturer due to its newly purchased nature. Upon expiry of calibration, both equipments will be calibrated in-house using Brüel & Kjær (B&K) calibrator model no 4226 while the calibration frequency will not exceed 2 years. The 4226 calibrator is annually calibrated by its manufacturer under the accreditation of United Kingdom Accreditation Service. The in-house calibration that has been undertaken can be traced back to the National Physical Laboratory. The calibration certificates for the noise equipments are given in **Appendix E**.

4.2.3 Monitoring Procedures

- The SLM and battery were checked to ensure that they are in proper condition. The SLM was set on a tripod at 1.2m above ground and at least 1m from the exterior of the building façade;
- Before conducting the measurement, the SLM was calibrated by an acoustical calibrator;
- Measurement parameter was set to A-weighted sound pressure level. The time weighting was set in fast response and the time period of measurement at 30 minutes;
- Wind speed was checked during noise monitoring to ensure the steady wind speed does not exceed 5m/s, or wind with gusts does not exceed 10m/s;
- Any abnormal conditions that generated intrusive noise during the measurement was recorded on the field record sheet;
- After each measurement, the equivalent continuous sound pressure level (L_{eq}), L_{10} and L_{90} were recorded on the field record sheet;
- After conducting the measurement, the SLM was calibrated by an acoustical calibrator; and
- The SLM was re-calibrated by the acoustical calibrator to confirm that there is no significant drift of reading. Measurements shall be accepted as valid only if the calibration levels before and after the noise measurement agrees to within 1.0 dB.

4.3 Monitoring Results and Observations

4.3.1 Weather Condition

The weather condition was mainly sunny during the noise monitoring period in the reporting month.

4.3.2 Noise Monitoring Results

Non-restricted Hours

Monitoring of the construction noise level was conducted during non-restricted hours on 6, 12, 18 and 29 May 2009 at TLLF(a). All monitoring data and graphical presentation of the monitoring results are provided in **Appendix F** and are summarised in **Table 4-4**. The graphical presentation of the monitoring results over past four months (February to May 2009) are also provided in **Appendix F**.

Table 4-4 Summary of impact noise monitoring in the reporting month

Date	Set	Start Time	End Time	Baseline* (Same period of the Day-time)	Impact Monitoring Result*	Impact Noise* after baseline correction	Limit Level dB(A)
				Leq (30-min), dB(A)	Leq (30-min), dB(A)	Leq (30-min), dB(A)	
6-May-09	First	13:10	13:40	74	69	/	70
12-May-09	First	11:35	12:05	74	69	/	
18-May-09	First	09:20	09:50	74	73	/	
	Second	10:05	10:35	74	72	/	
29-May-09	First	09:05	09:35	74	73	/	
	Second	10:05	10:35	74	72	/	

Note(*): Façade correction was included.

Restricted Hours

No night works were carried out during the reporting month.

4.3.3 Exceedance of Limit Levels for Construction Noise

Two (2) limit level exceedance for noise measurement during non-restricted hours was recorded on 18 and 29 May 2009. On-site observations during the noise monitoring revealed that the noise source was mainly the traffic noise along Tuen Mun Road although it was also observed that the Contractor was undertaking the noise barriers construction works.

Together with the on-site observations and interpretation from the monitoring results, construction noise was considered insignificant and below the noise limit level. It was therefore concluded that the noise exceedance was not related to the construction activities. No further actions were applicable. It was however recommended that the Contractor shall maintain the existing practices stipulated in the EIA report in order to minimise the potential noise impact in future.

4.3.4 General Observations

The construction site had been under normal operation during the noise monitoring period and no unusual operation was observed. Traffic noise had been noticed at the monitoring location during the noise monitoring period.

5 Landscape and Visual Monitoring

5.1 Landscape and Visual Impact Monitoring Requirements

Monitoring Requirement

In accordance with the EM&A Manual, a landscape auditor, as a member of the ET, is responsible for conducting the baseline review and monitoring the implementation of the landscape and visual mitigation measures during construction phase in accordance with the EIA report. Purposes of the review are:

- to check the status of the landscape resources within, and immediately adjacent to, the construction sites and works areas;
- to determine whether any change has occurred to the status of the landscape resources since the EIA;
- to determine whether amendments in the design of the landscape and visual mitigation measures are required for those changes; and
- to recommend any necessary amendments to the design of the landscape and visual mitigation measures.

The design, implementation and maintenance of landscape and visual mitigation measures shall be checked monthly to ensure that they are fully required. Any potential conflicts between the proposed landscape measures and any other project works or operational requirements shall also be recorded for the Contractor to resolve in early stage, without compromising the intention of the mitigation measures.

Monitoring Parameters

The components of assessed parameter of landscape resource is summarised below:

- Landscape Resource along the roadside planting at Tsing Tin Interchange (LR1); and
- Landscape Resource at Castle Peak Road (San Hui) Park (LR2).

Audit Frequency

The landscape and visual monitoring and audit shall be undertaken once a month throughout the construction period and operational phase.

Audit Location

The landscape and visual monitoring and audit shall be conducted throughout the entire site area.

5.2 Audit Results

In the reporting month, landscape and visual site audit in accordance with the requirements stipulated in the EM&A manual was conducted on 29 May 2009.

In accordance with the Clause 2.7 of the EP, seven numbers of trees (tree no. 1, 16, 35, 63, 69, 169 and 411) within the site shall be transplanted to their designed transplanted locations prior to the operational phase of the Project. Tree no.63 was dead after transplanting in March 2009 and tree no. 69 had been transplanted to new transplanting location in April 2009 and shown in **Appendix G**. Status of other six trees was no significant change during the reporting period and their respective mitigation measures was described in the previous monthly EM&A report. Status of the trees including their respective mitigation measures is summarised in **Table 5-1**.

Table 5-1 Status of tree transplantation

Tree no.	Location	Botanical Name	Status	Measures
1	LR1	<i>Melaleuca quinquenervia</i> 白千層	Fell by Typhoon	To be compensated by a tree at designated

Tree no.	Location	Botanical Name		Status	Measures
					location
16	LR1	<i>Melaleuca quinquenervia</i>	白千層	Fell by Typhoon	To be compensated by a tree at designated location
35	LR1	<i>Melaleuca quinquenervia</i>	白千層	Fell by Typhoon	To be compensated by a tree at designated location
63	LR1	<i>Gossampinus malabarica</i>	木棉	Dead after transplanting	To be compensated by a tree at designated location
69	LR1	<i>Melia azedarach</i>	森樹	Completion of relocation to new transplanting location	Not applicable
169	LR2	<i>Melaleuca quinquenervia</i>	白千層	Fell by Typhoon	To be compensated by a tree at designated location
411	LR2	<i>Melaleuca quinquenervia</i>	白千層	Completion of interim transplant within the site	To be transplanted at designated location

In accordance with Tree Assessment Schedule in Appendix 10.1 of the EIA Report, forty-seven trees of LR1 and LR2 would be affected as a result of the construction works. Seven of them, as described above, were proposed to be transplanted to their designated locations before operational phase, while the remaining forty trees were proposed to be felled during the construction phase. No significant change on their status was noted during the reporting period.

Compensatory planting of forty-seven number of trees prior the operational phase, as required in the Clause 2.8 of the EP, will be carried out after the consultation by LCSD. Observations during the monthly inspection summarized in **Table 5-2**.

Table 5-2 Status of forty trees to be affected during the construction stage

ID No.	Tree affected			Current Status
	No.	Botanical Name		
LR1	9	<i>Acacia confusa</i>	台灣相思	Transplanted to Siu Lang Shui Road
	10	<i>Acacia confusa</i>	台灣相思	Transplanted to Siu Lang Shui Road
	15	<i>Acacia confusa</i>	台灣相思	Transplanted to Siu Lang Shui Road
	17	<i>Acacia confusa</i>	台灣相思	Felled
	31	<i>Acacia confusa</i>	台灣相思	Felled
	32	<i>Acacia confusa</i>	台灣相思	Felled
	33	<i>Hibiscus tiliaceus</i>	黃槿	Felled
	34	<i>Hibiscus tiliaceus</i>	黃槿	Felled
	45	<i>Acacia confusa</i>	台灣相思	Felled
	46	<i>Thevetia peruviana</i>	黃花夾竹桃	Felled by Typhoon
	47	<i>Acacia confusa</i>	台灣相思	Felled
	48	<i>Hibiscus tiliaceus</i>	黃槿	Transplanted to Siu Lang Shui Road

ID No.	Tree affected		Current Status
	No.	Botanical Name	
	49	<i>Acacia confusa</i> 台灣相思	Felled
	50	<i>Hibiscus tiliaceus</i> 黃槿	Transplanted to Siu Lang Shui Road
	51	<i>Hibiscus tiliaceus</i> 黃槿	Transplanted to Siu Lang Shui Road
	52	<i>Hibiscus tiliaceus</i> 黃槿	Felled
	53	<i>Acacia confusa</i> 台灣相思	Transplanted to Siu Lang Shui Road
	54	<i>Hibiscus tiliaceus</i> 黃槿	Transplanted to Siu Lang Shui Road
	55	<i>Hibiscus tiliaceus</i> 黃槿	Felled
	56	<i>Hibiscus tiliaceus</i> 黃槿	Transplanted to Siu Lang Shui Road
	57	<i>Hibiscus tiliaceus</i> 黃槿	Transplanted to Siu Lang Shui Road
	58	<i>Acacia confusa</i> 台灣相思	Felled
	59	<i>Hibiscus tiliaceus</i> 黃槿	Transplanted to Siu Lang Shui Road
	60	<i>Acacia confusa</i> 台灣相思	Felled
	61	<i>Melaleuca quinquenervia</i> 白千層	Transplanted to Siu Lang Shui Road
	62	<i>Acacia confusa</i> 台灣相思	Felled
	64	<i>Hibiscus tiliaceus</i> 黃槿	Felled
	65	<i>Melia azedarach</i> 森樹	Felled
	293	<i>Hibiscus tiliaceus</i> 黃槿	Felled
LR2	155	<i>Acacia confusa</i> 台灣相思	Felled
	156	<i>Acacia confusa</i> 台灣相思	Felled
	163	<i>Melaleuca quinquenervia</i> 白千層	Felled
	165	<i>Acacia confusa</i> 台灣相思	Felled
	167	<i>Acacia confusa</i> 台灣相思	Felled
	168	<i>Acacia confusa</i> 台灣相思	Felled
	170	<i>Hibiscus tiliaceus</i> 黃槿	Felled
	171	<i>Hibiscus tiliaceus</i> 黃槿	Felled
	172	<i>Acacia confusa</i> 台灣相思	Felled
	173	<i>Acacia confusa</i> 台灣相思	Felled
	174	<i>Acacia confusa</i> 台灣相思	Felled

Thirty-five numbers of trees, which shall be retained in the site according to the Tree Assessment Schedule in Appendix 10.1 of the EIA Report, were damaged due to the typhoons prior to the commencement of the construction.

Based on the updated information provided by the contractor and the site inspections, no significant change on the tree status was noted during the reporting month.

5.3 Implementation Status of Consultation Phase Landscape and Visual Mitigation Measures

The design, implementation and maintenance of landscape and mitigation measures, listed in Table 8.2 of the EM&A manual, were checked during the monthly site audit. No non-compliance has been triggered. Summary of the implementation status of Construction Phase Landscape and Visual Mitigation Measures is presented in the Environmental Mitigation Implementation Schedule (EMIS) in **Appendix H**.

5.4 Recommendations, Corrective Actions and Outstanding Issues

The recommendations, corrective actions or outstanding issues in relation with the landscape and visual monitoring are as follows:

- Tree Survey and Felling Plans and Tree Schedule should be revised in accordance with actual conditions on site, such as tree location and missing trees, for future monitoring;
- The Contractor was reminded to properly store, segregate and dispose of the felled trees;
- The Contractor was reminded to water and fertilise the trees regularly and submit the records of the works to RE;
- When retained trees were prone to be disturbed by nearby construction works, protective fencing should be erected around the trees before commencement of works;
- Where construction of protective fencing was impractical, the trunks of retained trees should be protected from abrasion by wrapping with hessian sacking, and strapping with pallet timbers secured with wire;
- Any debris and wood produced as a result of pruning, felling and cavity work performed on trees should be collected and removed from site properly; and
- The Contractor was reminded to keep 7m protect zone and properly fenced for tree no.69;
- The Contractor was reminded to avoid trunks damage during the construction works and, takes the proper remedial measures immediately and tree protection when damage was observed; and
- The Contractor was reminded to avoid the materials storage too close to the trees.

6 Waste Disposal

The estimated amounts of different types of waste generated by the activities of the Project in the month are shown in **Table 6-1**. It was advised from the Contractor that determination of the actual amount of wastes generation is still in progress so the relevant information will be presented on the next EM&A report. Actual amounts of waste generated in April 2009 are shown in **Table 6-2**. The monthly summary waste flow table is provided in **Appendix I**.

Table 6-1 Estimated amounts of waste generated in the reporting month

Waste Type	Estimated Amount	Actual Amount	Disposal Locations
Inert C&D Waste	820 m ³	To be presented in next monthly report	Disposal of at fill bank at Tuen Mun Area 38
Metals	4 kg		Recycle collector
Paper/cardboard packaging	12 kg		Recycle collector
Chemical Waste	0 kg		Disposal of at SENT landfill
General Refuse	5 m ³		Disposal of at WENT landfill

Table 6-2 Actual amounts of waste generated in previous month (April 2009)

Waste Type	Estimated Amount	Actual Amount	Disposal Locations
Inert C&D Waste	330 m ³	330 m ³	Disposal of at fill bank at Tuen Mun Area 38
Metals	4 kg	4 kg	Recycle collector
Paper/cardboard packaging	15 kg	15 kg	Recycle collector
Chemical Waste	500 kg	500 kg	Disposal of at SENT landfill
General Refuse	5 m ³	5 m ³	Disposal of at WENT landfill

7 Environmental Performance

7.1 Environmental Site Inspection

Environmental site inspections were carried out on a weekly basis to monitor environmental issues on the construction sites to ensure that all mitigation measures were implemented timely and properly. The site inspections were carried out on 6, 14, 21 and 29 May 2009. A summary of the site inspections is presented in **Table 7-1**.

Table 7-1 Key findings of weekly environmental site audit in the reporting month

Inspection Date	Key Observations and Recommendations	CT's Response / Environmental Outcome	Follow up Status / Closed Date
Water Quality Mitigation Measures			
21 May 09	Washing of site exit was observed outward to the road. The Contractor was reminded to spray inward to the site.	Agreed with the ET's advice	Water was sprayed inward the site; closed on 21 May 09
Waste / Chemical Waste Management			
6 May 09	Housekeeping at the South Bound of the site should be improved. The Contractor was reminded to clean the u-channel in routine practice.	Agreed with the ET's advice	Housekeeping had been improved and u-channel had been cleaned; closed on 14 May 09

7.2 Non-Compliance Record

There was no non-compliance record identified in the reporting month.

7.3 Complaint Record

There was no environmental complaint received in the reporting month

7.4 Notification of Summons and Successful Prosecution

No summons or prosecutions related to environmental issues were received or made against the Project in the reporting month.

7.5 Review of Reasons of Non-Compliance

There was no non-compliance identified during the reporting month so review of the non-compliance was not required.

8 Future Key Issues

8.1 Key Issues for the Coming Month

Key issues to be considered in the forth-coming month include:

- Dust generation from activities on-site, such as vehicular movements along unpaved area, excavation and demolition;
- Noise impact from operating equipment and night works activities;
- Uncontrolled water discharge into nearby water body;
- Storage and using of chemicals/fuel and chemical waste/waste oil on site;
- Disposal of construction waste; and
- Tree maintenance.

8.2 Solid and Liquid Waste Management Status

Based on the findings of the weekly site inspection, the contractor's performance in terms of solid and liquid waste management was carried out in accordance with the requirements stipulated in the EIA report. Solid waste and liquid waste were disposed of properly. Existing practices should be continued.

8.3 Effectiveness and Efficiency of Mitigation Measures

Based on the environmental monitoring results, effectiveness and efficiency of the mitigation measures implemented were found satisfactory. Existing practices should be continued.

8.4 Environmental Monitoring Program for the Forth-coming Month

Environmental monitoring and audit will be carried out in accordance with the requirements stipulated in the EM&A manual. Tentative air, noise, landscape and visual monitoring as well as weekly site audit schedule for the forth-coming month with respect to the construction programme is shown in **Appendix J**.

The construction programme for the coming month is shown in **Table 8-1**.

Table 8-1 Tentative programme of construction works

Month	Details of Construction Works	
June 2009	<ul style="list-style-type: none"> ▪ Site clearance ▪ Construct ion of noise barrier footing ▪ Construction of the sign gantry footing 	<ul style="list-style-type: none"> ▪ Fill slope re-compaction ▪ Drainage and road re-construction ▪ Road pavement & drainage for widen lane

9 Conclusions and Recommendations

9.1 Conclusions

The construction phase of the Project was commenced on 2 October 2008. The EM&A programme has been implemented since then, including air quality, noise, landscape and visual and environmental site audits.

No complaint, summons or prosecution related to environmental issues was received during the reporting month.

Weekly environmental site audit was carried out during the reporting month. The major environmental concerns were related to air quality, water quality, landscape and visual impact, waste management as well as handling of chemical waste.

9.2 Recommendations

Impact monitoring will be continued to carry out in the following month and followed by the requirement stipulated in the EM&A manual. Attention shall be paid to environmental issues identified in EIA report and weekly site audit. Mitigation measures recommended in EIA report and Mitigation Measure Implementation Schedule shall be fully implemented.

Construction dust will continue to become a key environmental issue on windy days. The implemented construction dust mitigation measures should also be maintained and improved as necessary. Furthermore, landscape and visual impact mitigation measures such as sufficient protective fencing should be maintained and improved as necessary in order to protect the retained trees.


10 Reference

- 1) Maunsell Consultants Asia Ltd. December 2007. Quotation Ref No. Hy(S)Q/026/2006 Widening of Tuen Mun Road at Tsing Tin Interchange – Environmental Monitoring & Audit Manual.
- 2) Ove Arup & Partners Hong Kong Limited. September 2008. Contract No. HY/2007/14 Widening of Tsing Tin Interchange – Baseline Monitoring Report (Revision_6)

Appendix A

**Construction
Programme**

3 Month Rolling Programme

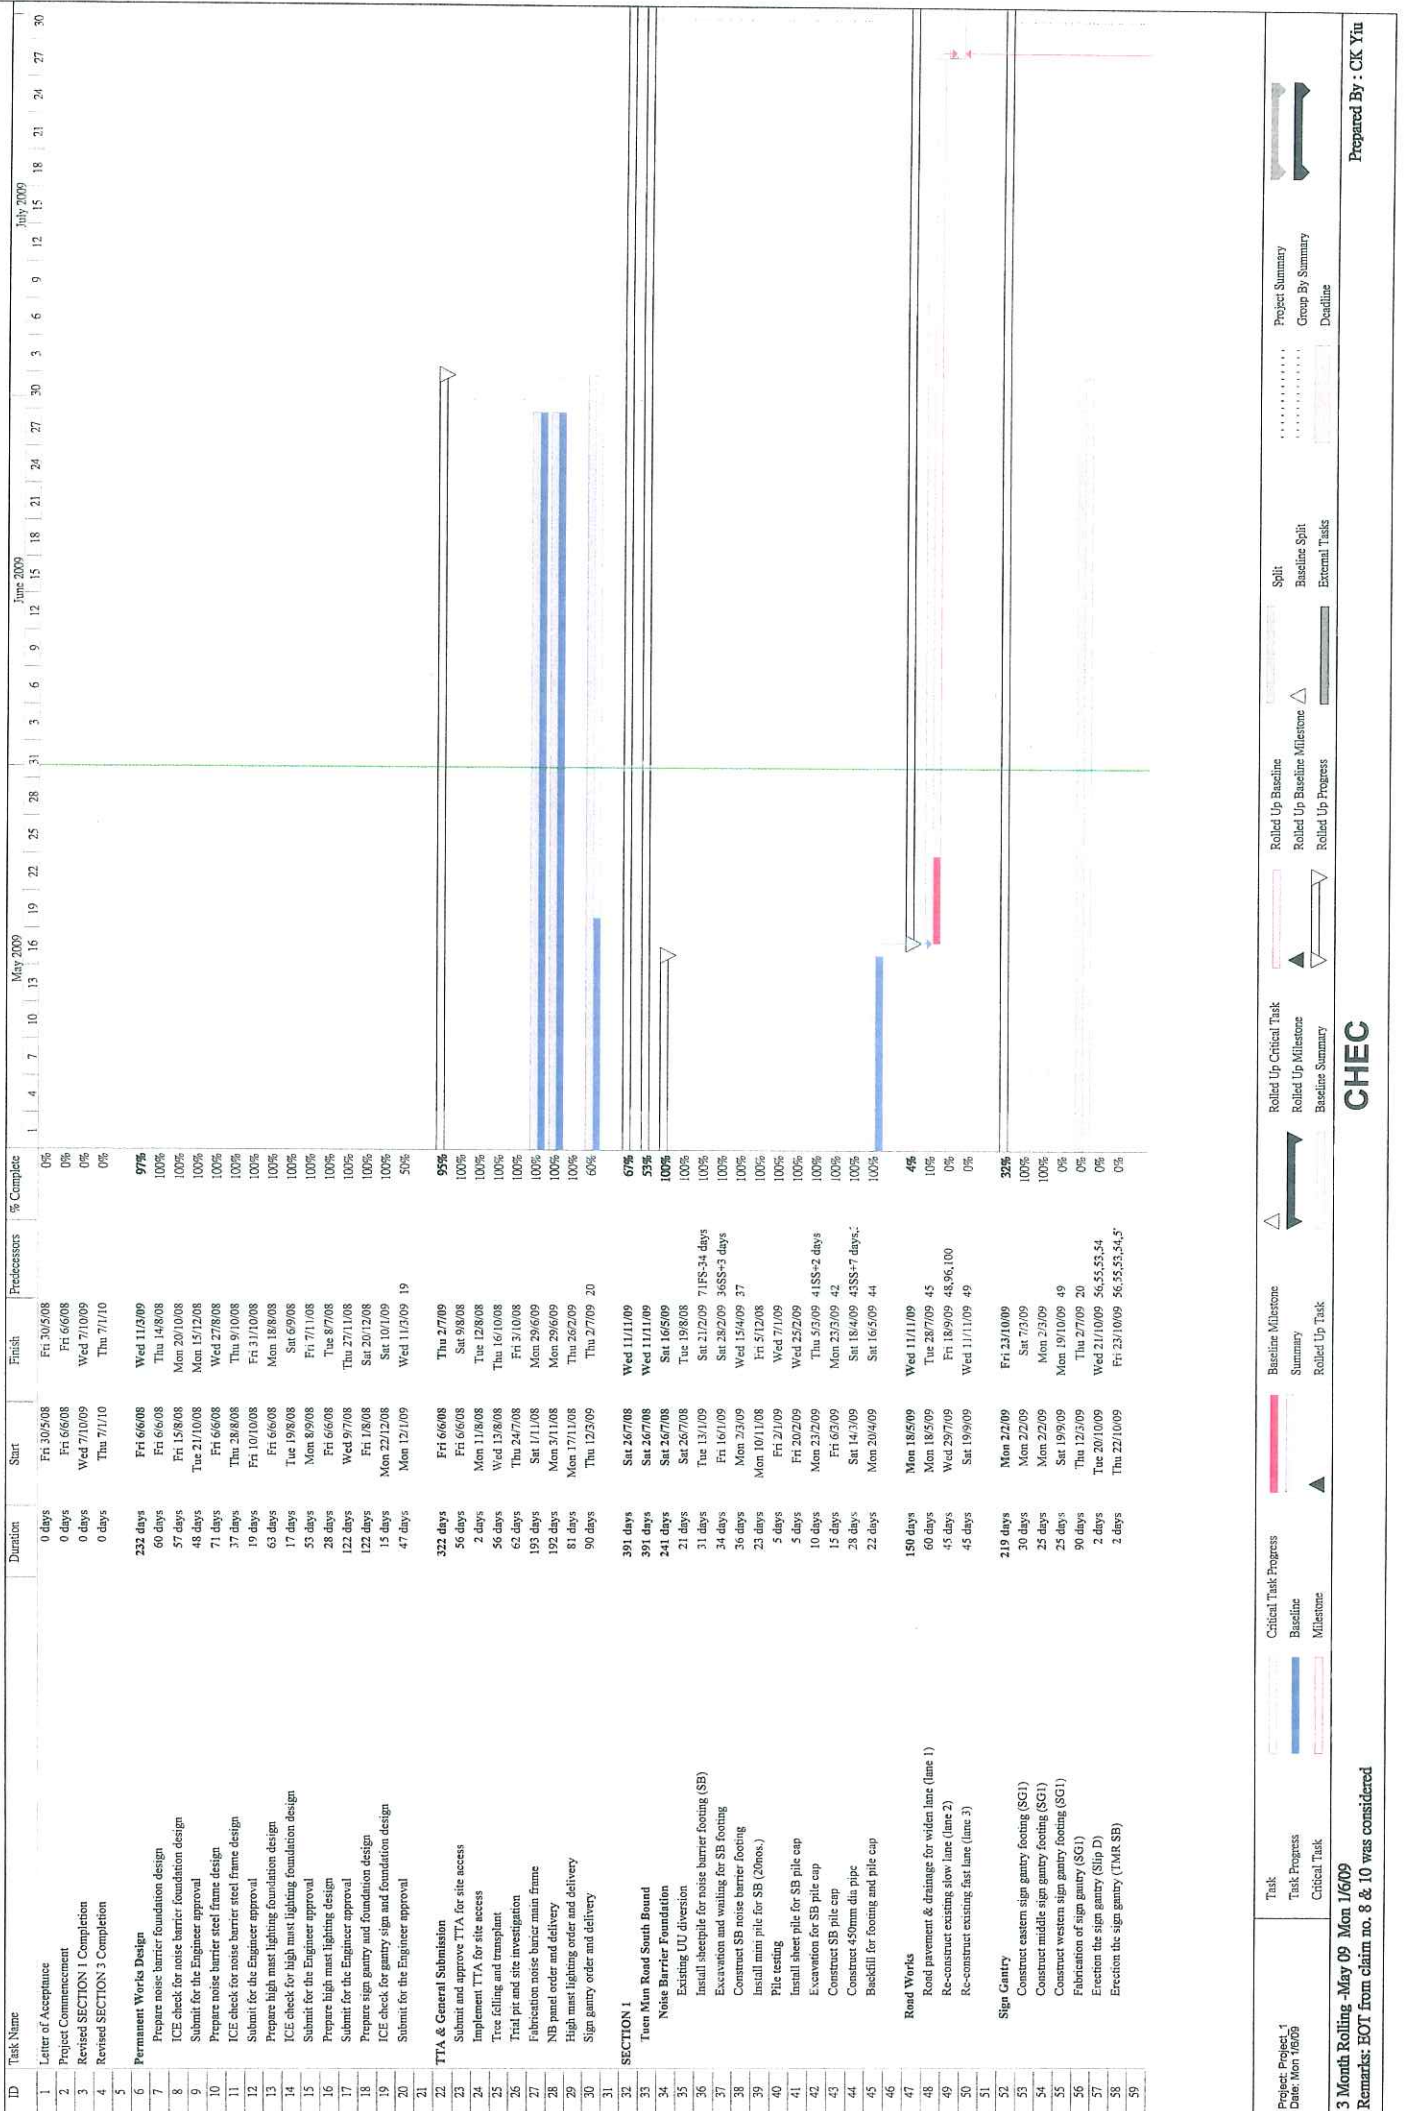


Project, Project 1
 Date: Mon 16/09

3 Month Rolling - May 09 - Mon 16/09
 Remarks: BOT from claim no. 8 & 10 was considered

Prepared By : CK Yin

3 Month Rolling Programme

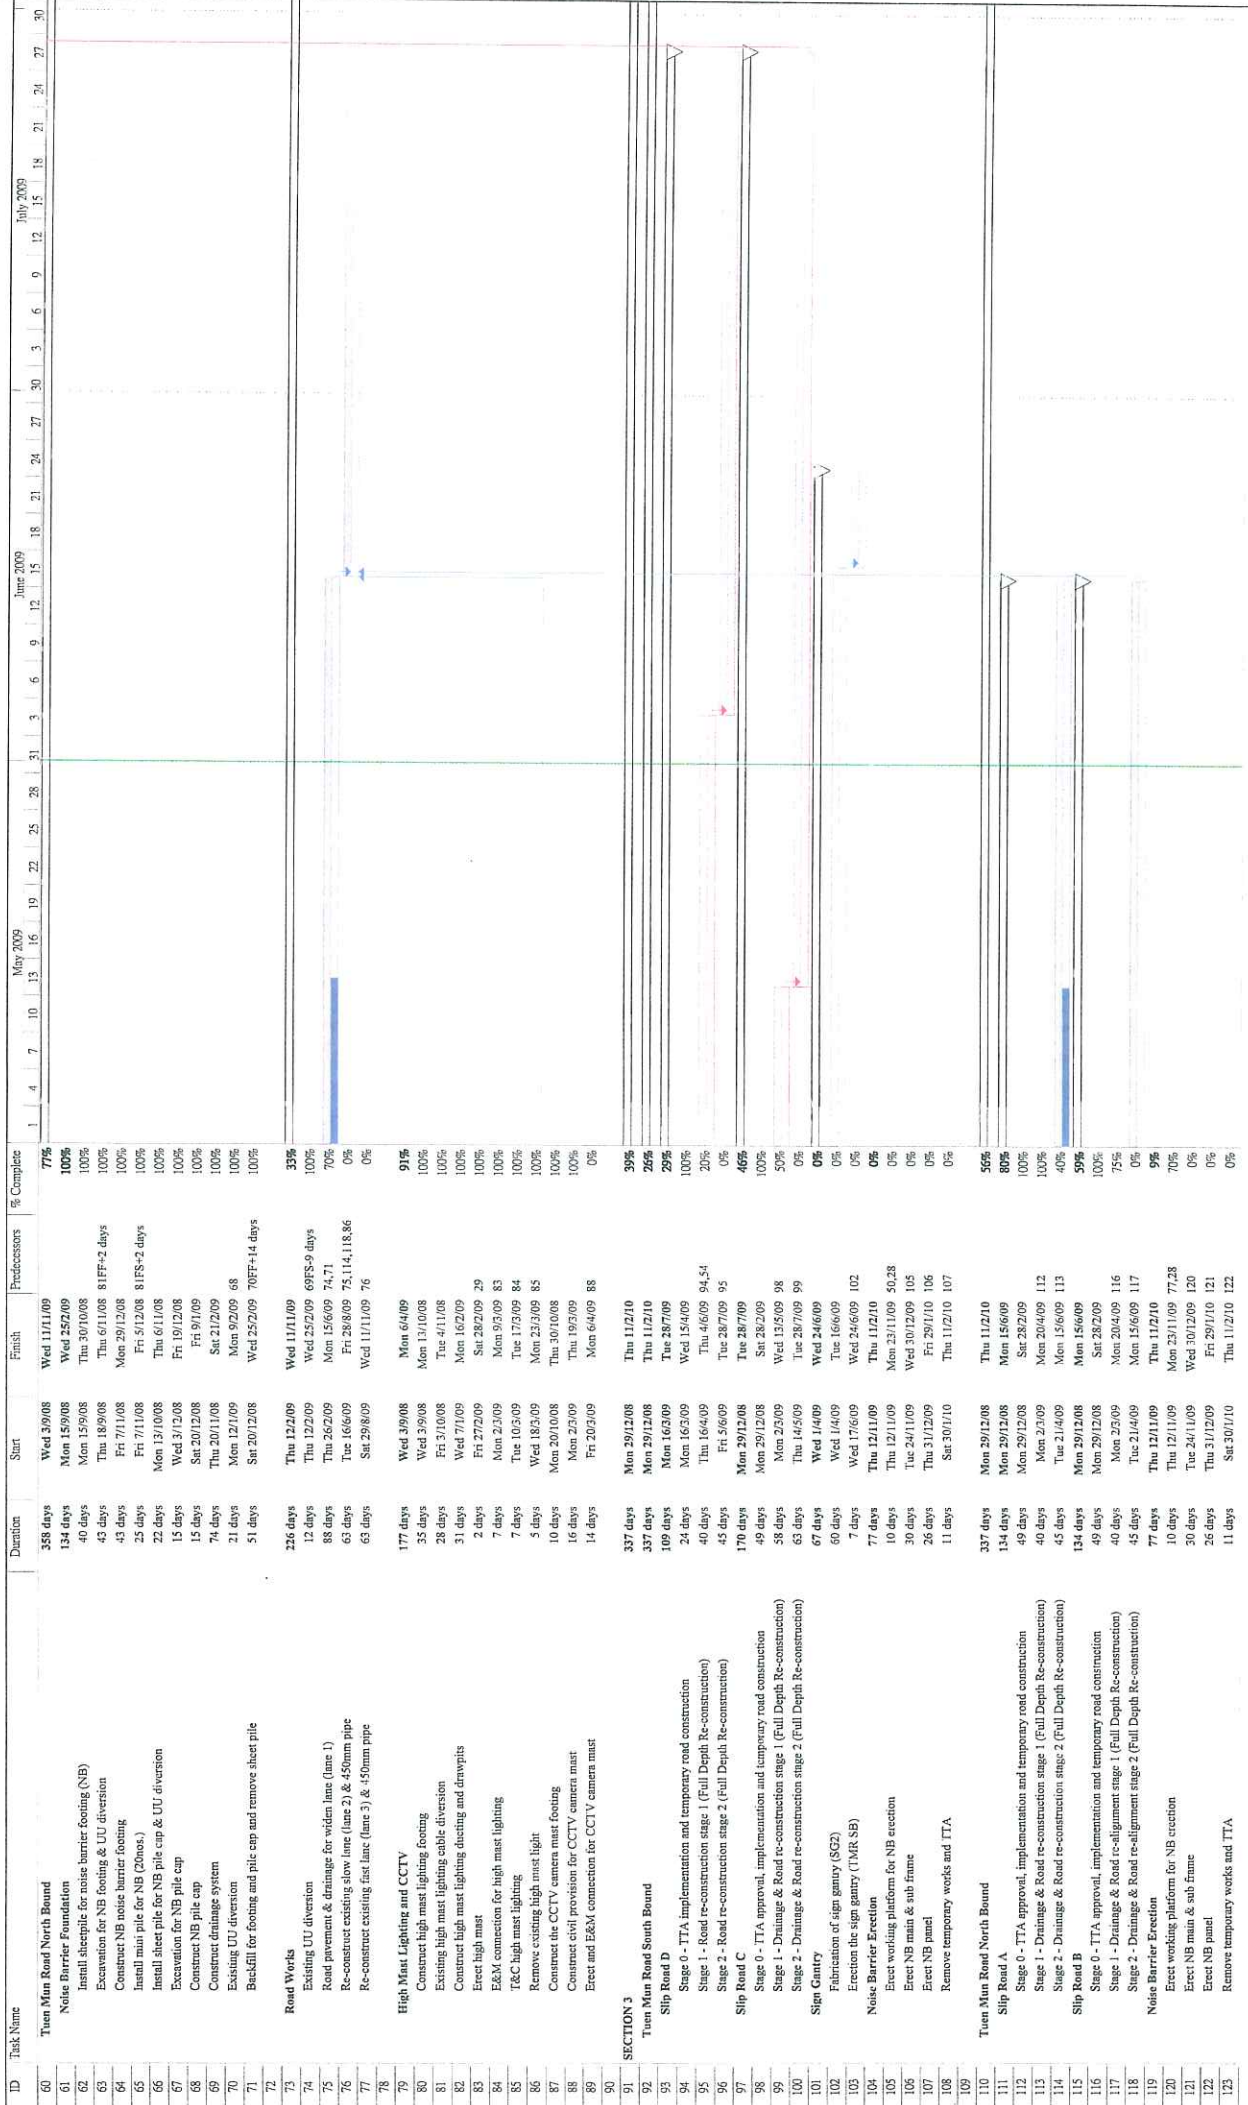

Project: Project 1
 Date: Mon 16/09

Task Progress:

Critical Task Progress:

Task Progress:

Critical Task:

Milestone:

Baseline Milestone:

Summary:

Roll Up Task:

Baseline Summary:

Roll Up Milestone:

Roll Up Baseline:

Roll Up Progress:

Roll Up Baseline Milestone:

Baseline Split:

External Tasks:

Split:

Project Summary:

Group By Summary:

Deadline:

Prepared By : CK Yiu

Appendix B

**Calibration
Spreadsheets of the
High Volume Samplers
and Calibration
Certificate of
Calibration Kit**



TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE.
 VILLAGE OF CLEVELAND, OH 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX
 WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date -. Feb 23, 2009 Rootsometer S/N 9833620 Ta (K) - 293
 Operator Tisch Orifice I.D. - 1378 Pa (mm) - 765.81

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.4180	3.2	2.00
2	NA	NA	1.00	0.9970	6.4	4.00
3	NA	NA	1.00	0.8930	7.9	5.00
4	NA	NA	1.00	0.8520	8.8	5.50
5	NA	NA	1.00	0.7030	12.8	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
1.0205	0.7197	1.4317	0.9958	0.7022	0.8748
1.0162	1.0192	2.0247	0.9915	0.9945	1.2371
1.0142	1.1357	2.2637	0.9896	1.1082	1.3831
1.0130	1.1890	2.3742	0.9885	1.1602	1.4506
1.0077	1.4334	2.8633	0.9832	1.3987	1.7495
Qstd slope (m) = 2.00826			Qa slope (m) = 1.25754		
intercept (b) = -0.01649			intercept (b) = -0.01008		
coefficient (r) = 0.99995			coefficient (r) = 0.99995		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

$$Vstd = \text{Diff. Vol} [(Pa - \text{Diff. Hg}) / 760] (298 / Ta)$$

$$Qstd = Vstd / \text{Time}$$

$$Va = \text{Diff Vol} [(Pa - \text{Diff Hg}) / Pa]$$

$$Qa = Va / \text{Time}$$

For subsequent flow rate calculations:


$$Qstd = 1/m \{ [\text{SQRT}(H2O(Pa/760) (298/Ta))] - b \}$$

$$Qa = 1/m \{ [\text{SQRT} H2O(Ta/Pa)] - b \}$$



TISCH ENVIROMENTAL, INC.
 145 SOUTH MIAMI AVE.
 VILLAGE OF CLEVES, OH 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX
 WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

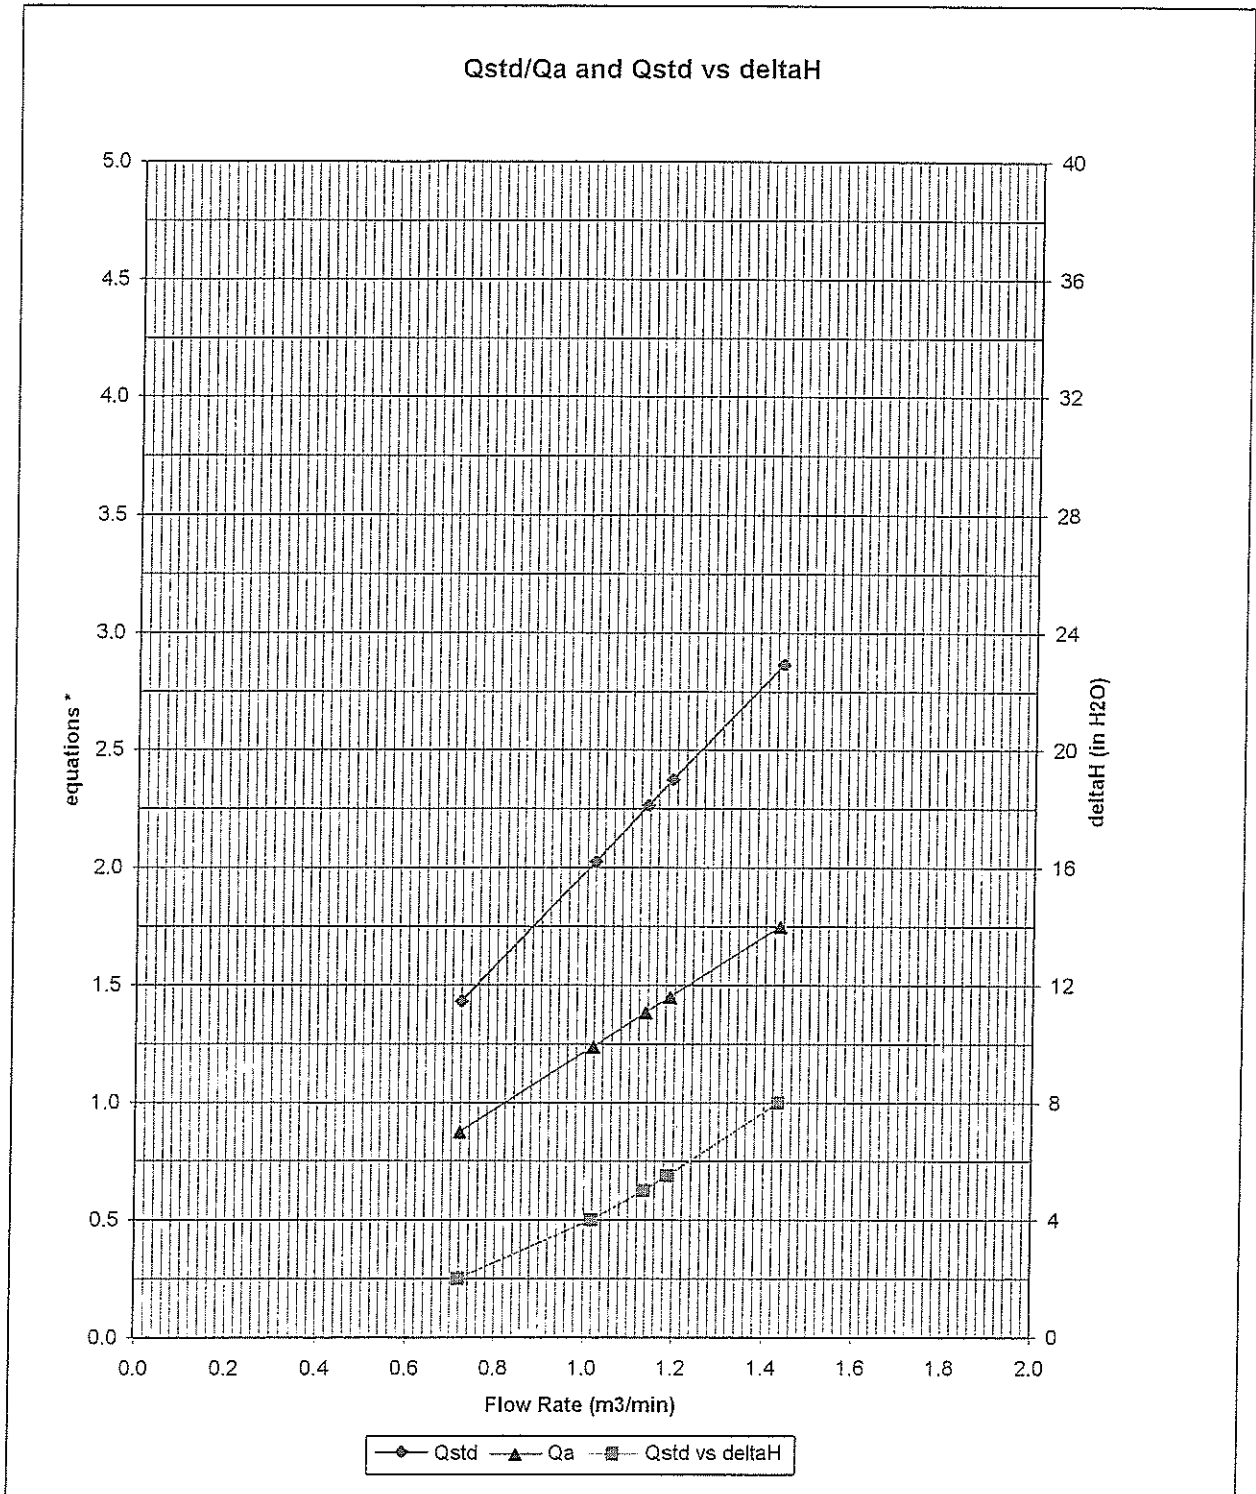

* y-axis equations:

Qstd series:
$$\sqrt{\Delta H \left(\frac{P_a}{P_{std}} \right) \left(\frac{T_{std}}{T_a} \right)}$$

Qa series:
$$\sqrt{(\Delta H (T_a / P_a))}$$

1378


Ove Arup Partners (Hong Kong) Limited

High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-09	Barometric pressure	761 mm Hg
Calibration due date	31-May-09	Tempature (°C)	23 °C
Sampler location	TT1-Roof,Kwong Choi Market	Tempature (K)	296 K
Sampler model	TE-5170	P _{std}	760 mm Hg
Sampler serial number	0521	T _{std}	298 K

Calibrator model	GMW-2535
Calibrator serial number	1378
Slope of the standard curve, m _s	2.00826
Intercept of the standard curve, b _s	-0.01649


Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	3.20	29.00	0.90	29.12
7	5.10	38.00	1.14	38.15
10	8.60	50.00	1.47	50.20
13	9.80	56.00	1.57	56.23
18	13.50	63.00	1.85	63.25

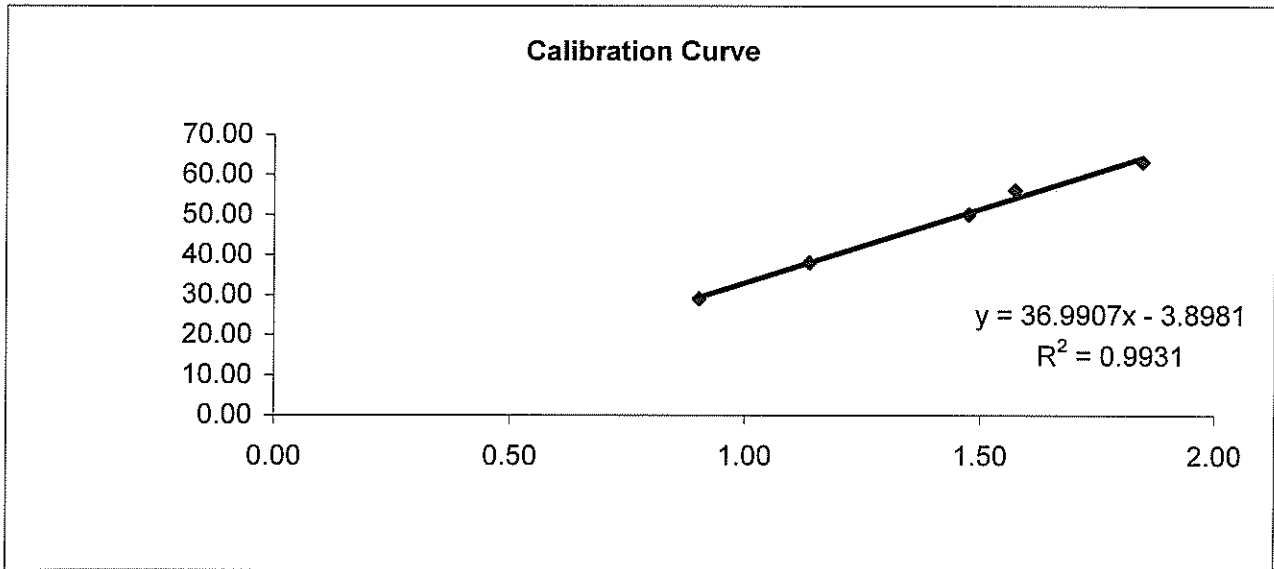


Linear Regression

Sampler slope (m) : **36.9907**
 Sampler intercept (b) : **-3.8981**
 Correlation coefficient (R²) : **0.9931**

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: 

Checked by: 

Date: 1-4-09


Date: 1-4-09

Ove Arup Partners (Hong Kong) Limited

High Volume Air Sampler Calibration Worksheet

Calibration date	1-Apr-09	Barometric pressure	761 mm Hg
Calibration due date	31-May-09	Temperature (°C)	23 °C
Sampler location	TT2 - G/F Tam Lee Lai Fun Memorial School	Temperature (K)	296 K
Sampler model	TE-5170	P _{std}	760 mm Hg
Sampler serial number	0523	T _{std}	298 K
Calibrator model	GMW-2535		
Calibrator serial number	1378		
Slope of the standard curve, m _s	2.00826		
Intercept of the standard curve, b _s	-0.01649		



Resistance Plate No.	Manometer Reading (inch H ₂ O)	Flow Recorder Reading (CFM)	Calculated Q _{std} (m ³ /min)	Continuous Flow Recorder Reading IC (CFM)
5	3.30	26.00	0.92	26.10
7	5.20	37.00	1.15	37.15
10	8.00	47.00	1.42	47.19
13	9.80	54.00	1.57	54.22
18	12.70	62.00	1.79	62.25

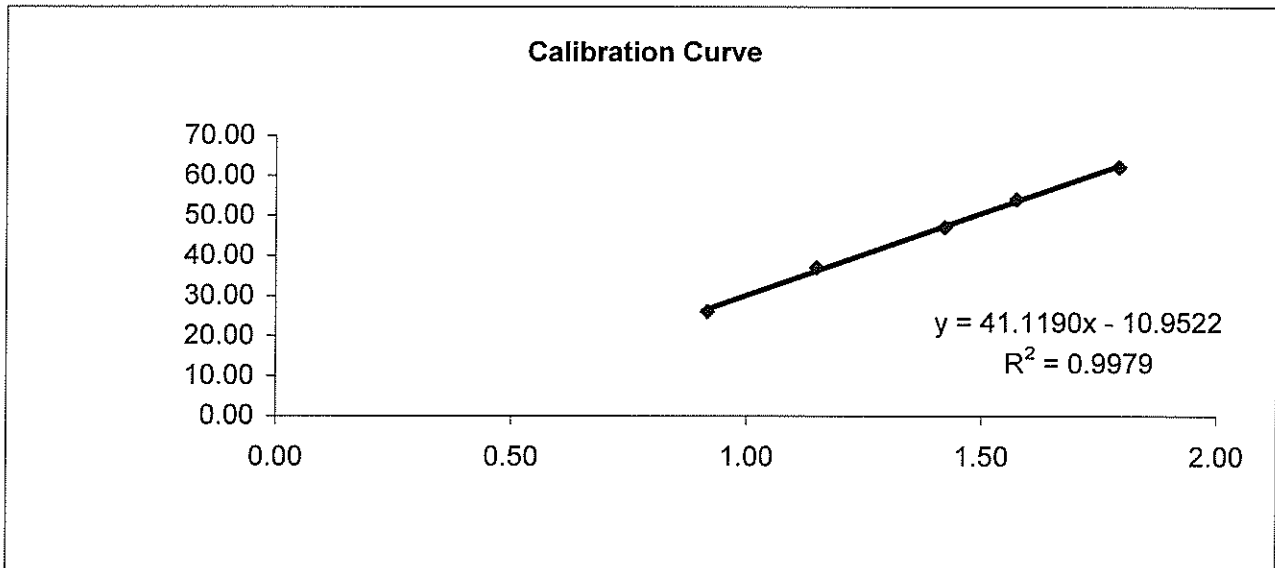

Linear Regression

Sampler slope (m) : **41.1190**
 Sampler intercept (b) : **-10.9522**
 Correlation coefficient (R²) : **0.9979**

Correlation coefficient is greater than 0.9900 and the calibration result is accepted.

Performed by: 
 Checked by: 

Date: 1-4-09
 Date: 1-4-09



Appendix C



**Impact Air Monitoring
Results**

**Contract No. Hy/2007/14 - Widening of Tuen Mun Road at Tsing Tin Interchange
Impact Air Monitoring Result - 1 hour TSP**

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Filter Weight (g)		TSP weight (g)	Flow Rate (m ³ /min)		Average Flow Rate (m ³ /min)	Elapse Time		Sampling Time	Total vol. (m ³)	AM1(a)	AM3(a)
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish				
OY58	May-09	6-May-09	TT1-1	Fine	Normal Operation	759.0	759.0	26.0	26.0	40.0	40.0	2.8450	2.8458	0.0008	1.1842	1.1842	1.1842	9594.31	9595.31	60.00	71.05	11.3	
OY59	May-09	6-May-09	TT1-2	Fine	Normal Operation	759.0	759.0	26.0	26.0	40.0	40.0	2.8221	2.8231	0.0010	1.1842	1.1842	1.1842	9595.31	9596.31	60.00	71.05	14.1	
OY60	May-09	6-May-09	TT1-3	Fine	Normal Operation	759.0	759.0	26.0	26.0	40.0	40.0	2.8195	2.8203	0.0008	1.1842	1.1842	1.1842	9596.31	9597.31	60.00	71.05	11.3	
OY55	May-09	6-May-09	TT2-1	Fine	Normal Operation	759.0	759.0	26.0	26.0	40.0	40.0	2.8797	2.8805	0.0008	1.2369	1.2369	1.2369	9171.18	9172.18	60.00	74.21		10.8
OY56	May-09	6-May-09	TT2-2	Fine	Normal Operation	759.0	759.0	26.0	26.0	40.0	40.0	2.8742	2.8750	0.0008	1.2369	1.2369	1.2369	9172.18	9173.18	60.00	74.21		10.8
OY06	May-09	6-May-09	TT2-3	Fine	Normal Operation	759.0	759.0	26.0	26.0	40.0	40.0	2.8650	2.8741	0.0091	1.2369	1.2369	1.2369	9173.18	9174.18	60.00	74.21		122.6
OY41	May-09	12-May-09	TT1-1	Fine	Normal Operation	757.0	757.0	29.0	29.0	40.0	40.0	2.8370	2.8379	0.0009	1.1775	1.1775	1.1775	9621.31	9622.31	60.00	70.65	12.7	
OY42	May-09	12-May-09	TT1-2	Fine	Normal Operation	757.0	757.0	29.0	29.0	40.0	40.0	2.8400	2.8410	0.0010	1.1775	1.1775	1.1775	9622.31	9623.31	60.00	70.65	14.2	
OY43	May-09	12-May-09	TT1-3	Fine	Normal Operation	757.0	757.0	29.0	29.0	40.0	40.0	2.9030	2.9040	0.0010	1.1775	1.1775	1.1775	9623.31	9624.31	60.00	70.65	14.2	
OY44	May-09	12-May-09	TT2-1	Fine	Normal Operation	757.0	757.0	29.0	29.0	40.0	40.0	2.8601	2.8610	0.0009	1.2308	1.2308	1.2308	9200.18	9201.18	60.00	73.85		12.2
OY45	May-09	12-May-09	TT2-2	Fine	Normal Operation	757.0	757.0	29.0	29.0	40.0	40.0	2.8949	2.8957	0.0008	1.2308	1.2308	1.2308	9201.18	9202.18	60.00	73.85		10.8
OY46	May-09	12-May-09	TT2-3	Fine	Normal Operation	757.0	757.0	29.0	29.0	40.0	40.0	2.8614	2.8624	0.0010	1.2308	1.2308	1.2308	9202.18	9203.18	60.00	73.85		13.5
OY65	May-09	18-May-09	TT1-1	Fine	Normal Operation	757.0	757.0	30.0	30.0	40.0	40.0	2.8218	2.8227	0.0009	1.1757	1.1757	1.1757	9648.31	9649.31	60.00	70.54	12.8	
OY66	May-09	18-May-09	TT1-2	Fine	Normal Operation	757.0	757.0	30.0	30.0	40.0	40.0	2.8593	2.8598	0.0005	1.1757	1.1757	1.1757	9649.31	9650.31	60.00	70.54	7.1	
OY67	May-09	18-May-09	TT1-3	Fine	Normal Operation	757.0	757.0	30.0	30.0	40.0	40.0	2.8357	2.8367	0.0010	1.1757	1.1757	1.1757	9650.31	9651.31	60.00	70.54	14.2	
OY08	May-09	18-May-09	TT2-1	Fine	Normal Operation	757.0	757.0	30.0	30.0	40.0	40.0	2.8409	2.8538	0.0129	1.2292	1.2292	1.2292	9227.18	9228.18	60.00	73.75		174.9
OY85	May-09	18-May-09	TT2-2	Fine	Normal Operation	757.0	757.0	30.0	30.0	40.0	40.0	2.8700	2.8708	0.0008	1.2292	1.2292	1.2292	9228.18	9229.18	60.00	73.75		10.8
OY86	May-09	18-May-09	TT2-3	Fine	Normal Operation	757.0	757.0	30.0	30.0	40.0	40.0	2.7831	2.7846	0.0015	1.2292	1.2292	1.2292	9229.18	9230.18	60.00	73.75		20.3
OY71	May-09	23-May-09	TT1-1	cloudy	Normal Operation	756.0	756.0	26.0	26.0	40.0	40.0	2.8549	2.8556	0.0007	1.1821	1.1821	1.1821	9675.31	9676.31	60.00	70.93	9.9	
OY72	May-09	23-May-09	TT1-2	cloudy	Normal Operation	756.0	756.0	26.0	26.0	40.0	40.0	2.8174	2.8184	0.0010	1.1821	1.1821	1.1821	9676.31	9677.31	60.00	70.93	14.1	
OY73	May-09	23-May-09	TT1-3	cloudy	Normal Operation	756.0	756.0	26.0	26.0	40.0	40.0	2.8735	2.8744	0.0009	1.1821	1.1821	1.1821	9677.31	9678.31	60.00	70.93	12.7	
OY68	May-09	23-May-09	TT2-1	cloudy	Normal Operation	756.0	756.0	26.0	26.0	40.0	40.0	2.8478	2.8485	0.0007	1.2350	1.2350	1.2350	9254.18	9255.18	60.00	74.10		9.4
OY69	May-09	23-May-09	TT2-2	cloudy	Normal Operation	756.0	756.0	26.0	26.0	40.0	40.0	2.8365	2.8370	0.0005	1.2350	1.2350	1.2350	9255.18	9256.18	60.00	74.10		6.7
OY70	May-09	23-May-09	TT2-3	cloudy	Normal Operation	756.0	756.0	26.0	26.0	40.0	40.0	2.8226	2.8231	0.0005	1.2350	1.2350	1.2350	9256.18	9257.18	60.00	74.10		6.7
OZ23	May-09	29-May-09	TT1-1	cloudy	Normal Operation	758.0	758.0	22.0	22.0	40.0	40.0	2.8316	2.8324	0.0008	1.1908	1.1908	1.1908	9702.31	9703.31	60.00	71.45	11.2	
OZ24	May-09	29-May-09	TT1-2	cloudy	Normal Operation	758.0	758.0	22.0	22.0	40.0	40.0	2.8470	2.8480	0.0010	1.1908	1.1908	1.1908	9703.31	9704.31	60.00	71.45	14.0	
OZ26	May-09	29-May-09	TT1-3	cloudy	Normal Operation	758.0	758.0	22.0	22.0	40.0	40.0	2.8593	2.8599	0.0006	1.1908	1.1908	1.1908	9704.31	9705.31	60.00	71.45	8.4	
OZ27	May-09	29-May-09	TT2-1	cloudy	Normal Operation	758.0	758.0	22.0	22.0	40.0	40.0	2.8650	2.8658	0.0008	1.2428	1.2428	1.2428	9281.18	9282.18	60.00	74.57		10.7
OZ28	May-09	29-May-09	TT2-2	cloudy	Normal Operation	758.0	758.0	22.0	22.0	40.0	40.0	2.8237	2.8246	0.0009	1.2428	1.2428	1.2428	9282.18	9283.18	60.00	74.57		12.1
OY47	May-09	29-May-09	TT2-3	cloudy	Normal Operation	758.0	758.0	22.0	22.0	40.0	40.0	2.8670	2.8678	0.0008	1.2428	1.2428	1.2428	9283.18	9284.18	60.00	74.57		10.7

Average	12.1	29.5
Max	14.2	174.9
Min	7.1	6.7

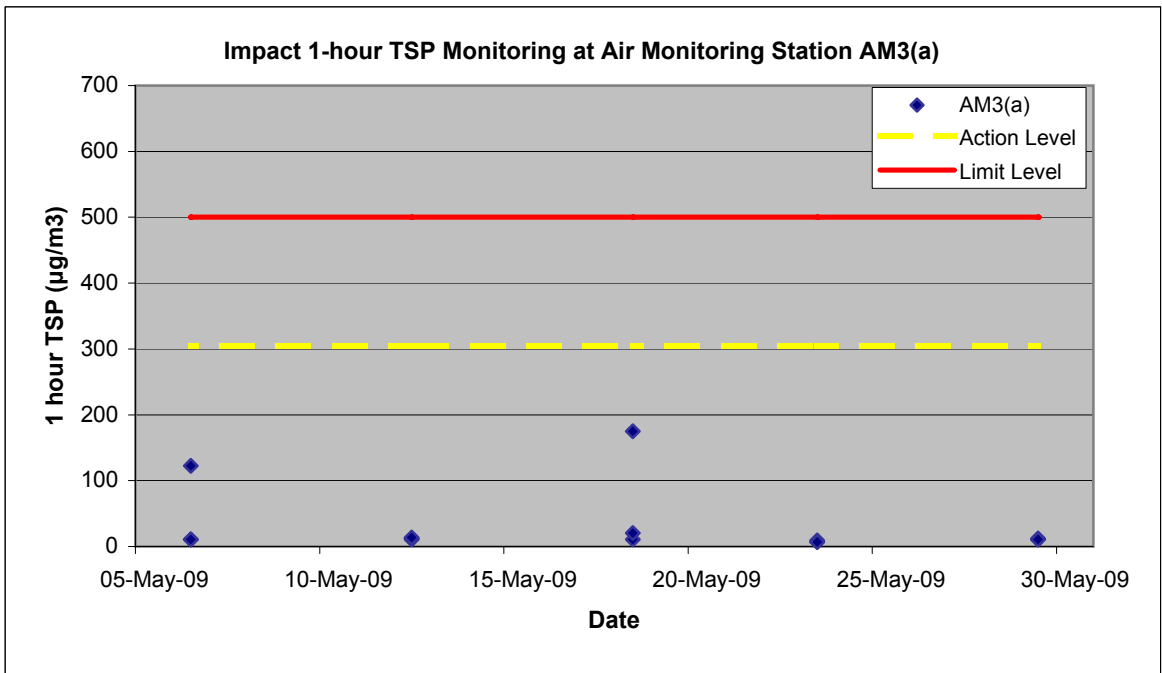
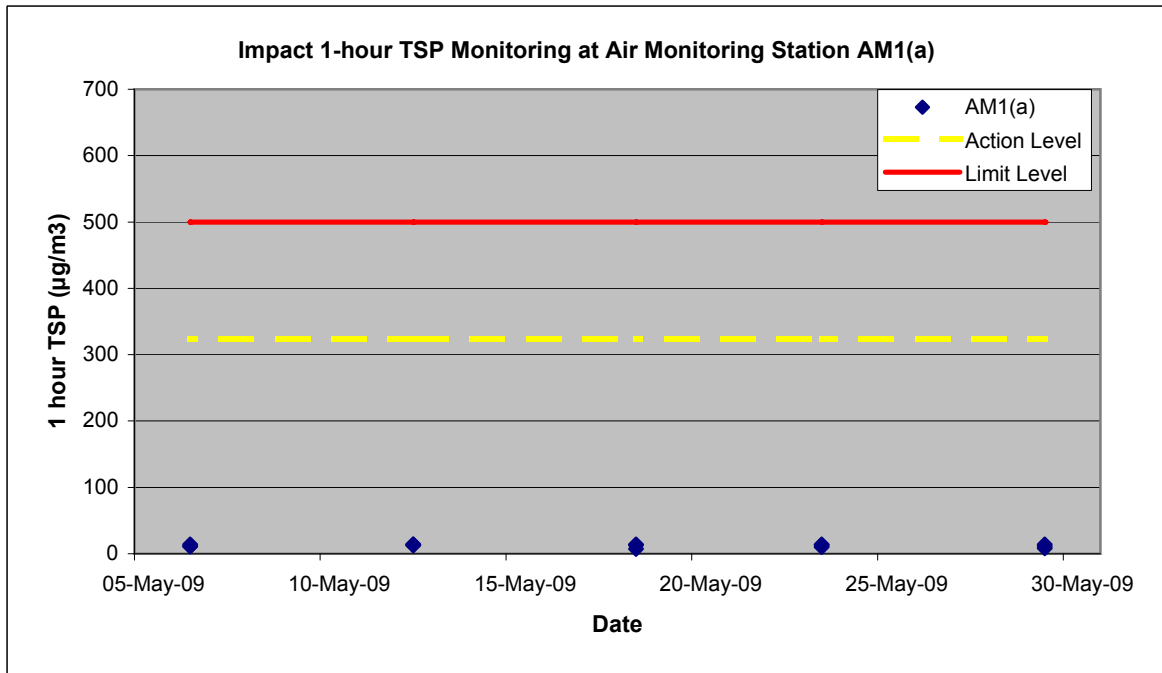


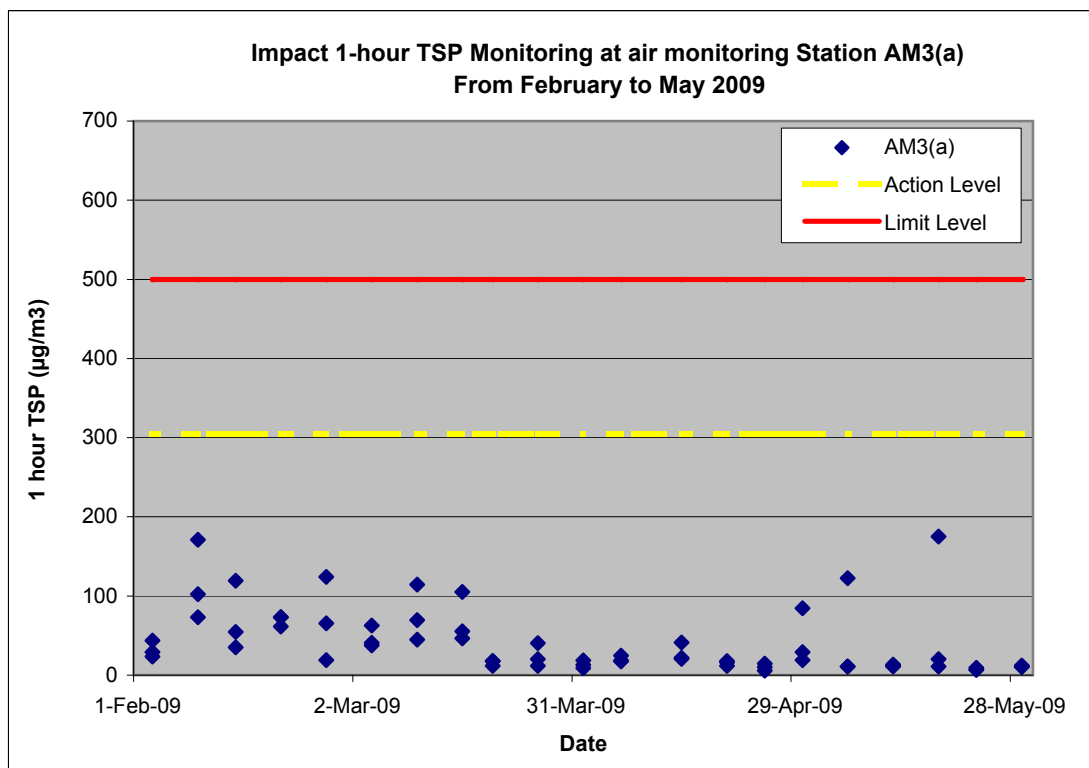
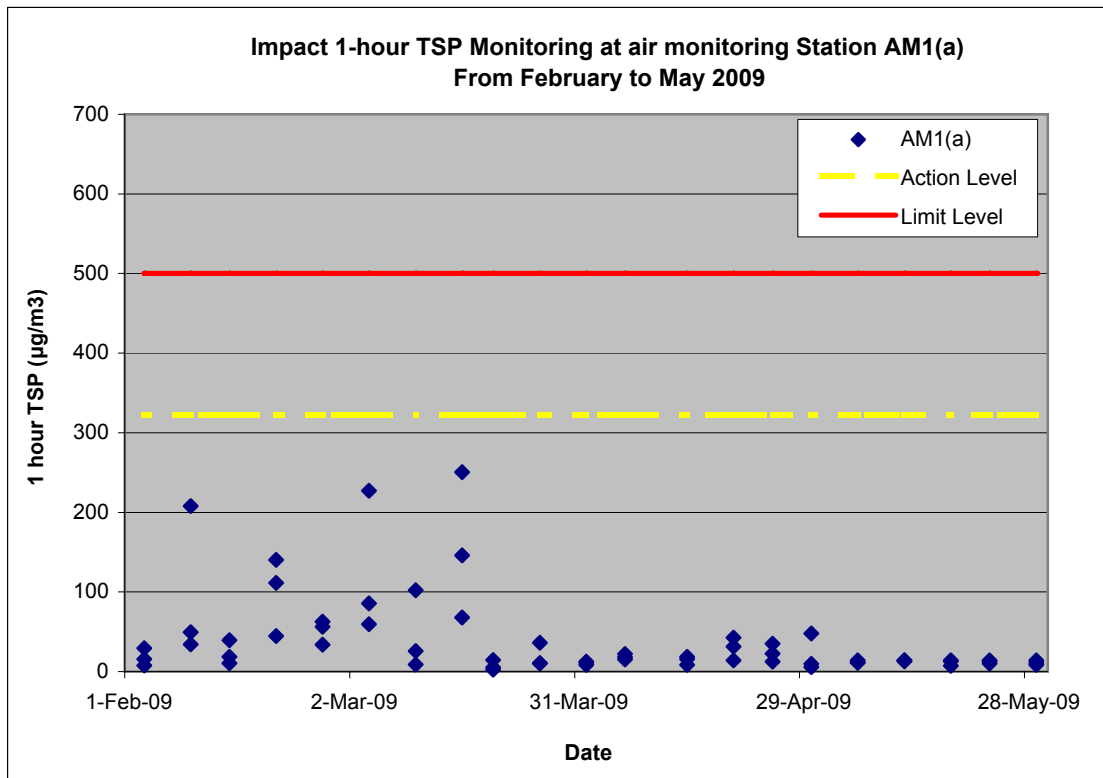


**Contract No. Hy/2007/14 - Widening of Tuen Mun Road at Tsing Tin Interchange
Impact Air Monitoring Result - 24 hours TSP**

Filter No.	Month	Date	Receptor No.	Weather condition	Site condition	Pressure (mmHg)		Temperature (oC)		Flow Recorder Reading (CFM)		Weight (g)		TSP weight (g)	Rate (m ³ /min)		Average Flow Rate (m ³ /min)	Elapse Time		Sampling Time	Total vol. (m ³)	AM1(a)	AM3(a)
						Initial	Final	Initial	Final	Initial	Final	Initial	Final		Initial	Final		Start	Finish				
OY18	May-09	4-May-09	TT1	Fine	Normal Operation	760.0	760.0	23.0	23.0	40.0	40.0	2.8815	2.9676	0.0861	1.1904	1.1904	1.1904	9570.31	9594.31	1440.00	1714.18	50.2	
OY17	May-09	4-May-09	TT2	Fine	Normal Operation	760.0	760.0	23.0	23.0	40.0	40.0	2.8630	2.9618	0.0988	1.2424	1.2424	1.2424	9147.18	9171.18	1440.00	1789.06		55.2
OY39	May-09	7-May-09	TT1	Fine	Normal Operation	757.0	757.0	22.0	23.0	40.0	40.0	2.8319	2.9165	0.0846	1.1901	1.1883	1.1892	9597.31	9621.31	1440.00	1712.45	49.4	
OY40	May-09	7-May-09	TT2	Fine	Normal Operation	757.0	757.0	22.0	23.0	40.0	40.0	2.8850	2.9529	0.0679	1.2422	1.2405	1.2414	9174.18	9200.18	1560.00	1936.51		35.1
OY62	May-09	13-May-09	TT1	Fine	Normal Operation	757.0	758.0	26.0	25.0	40.0	40.0	2.8488	2.9580	0.1092	1.1828	1.1853	1.1841	9624.31	9648.31	1440.00	1705.03	64.0	
OY63	May-09	13-May-09	TT2	Fine	Normal Operation	757.0	758.0	26.0	25.0	40.0	40.0	2.8532	2.8640	0.0108	1.2356	1.2379	1.2368	9203.18	9227.18	1440.00	1780.92		6.1
OY88	May-09	19-May-09	TT1	Fine	Normal Operation	756.0	756.0	28.0	28.0	40.0	40.0	2.8242	2.8689	0.0447	1.1785	1.1785	1.1785	9651.31	9675.31	1440.00	1697.04	26.3	
OY87	May-09	19-May-09	TT2	Fine	Normal Operation	756.0	756.0	28.0	28.0	40.0	40.0	2.8238	2.8781	0.0543	1.2317	1.2317	1.2317	9230.18	9254.18	1440.00	1773.65		30.6
OY97	May-09	25-May-09	TT1	Cloudy	Normal Operation	757.0	756.0	25.0	25.0	40.0	40.0	2.8321	2.9001	0.0680	1.1846	1.1839	1.1843	9678.31	9702.31	1440.00	1705.32	39.9	
OY98	May-09	25-May-09	TT2	Cloudy	Normal Operation	757.0	756.0	25.0	25.0	40.0	40.0	2.8395	2.9089	0.0694	1.2372	1.2366	1.2369	9257.18	9281.18	1440.00	1781.14		39.0
OZ16	May-09	30-May-09	TT1	Cloudy	Normal Operation	757.0	756.0	24.0	26.0	40.0	40.0	2.8458	2.9028	0.0570	1.1865	1.1821	1.1843	9705.31	9729.31	1440.00	1705.39	33.4	
OZ15	May-09	30-May-09	TT2	Cloudy	Normal Operation	757.0	756.0	24.0	26.0	40.0	40.0	2.8308	2.8880	0.0572	1.2389	1.2350	1.2370	9284.18	9308.18	1440.00	1781.21		32.1

Average	43.9	33.0
Max	64.0	55.2
Min	26.3	6.1

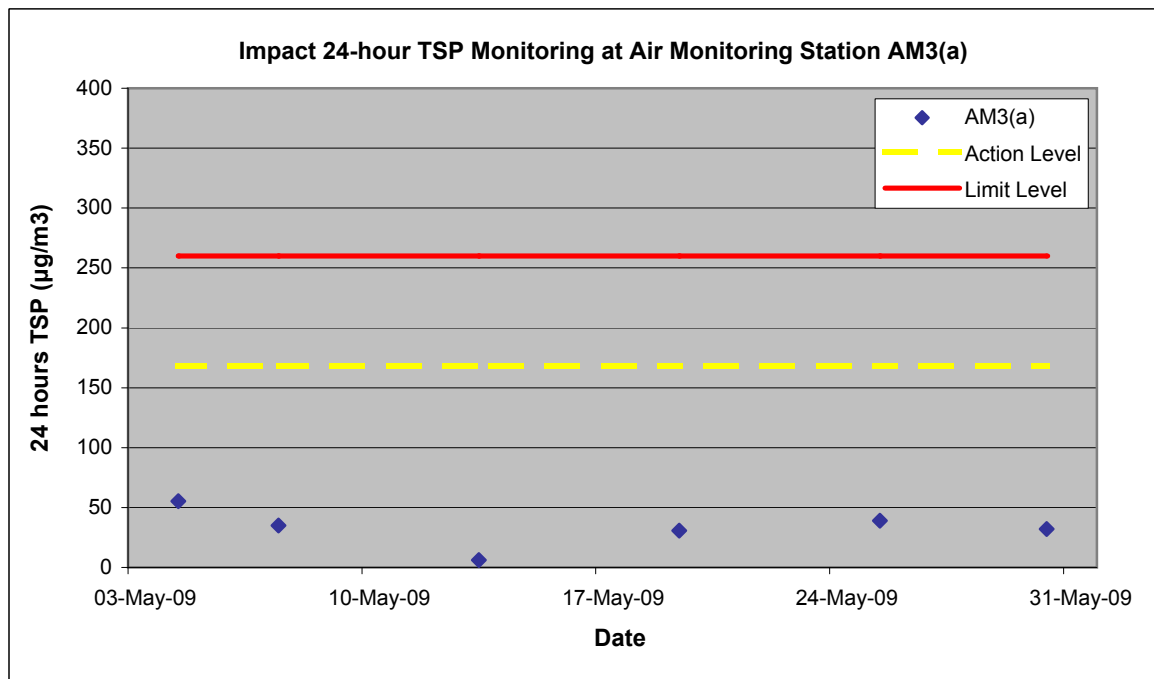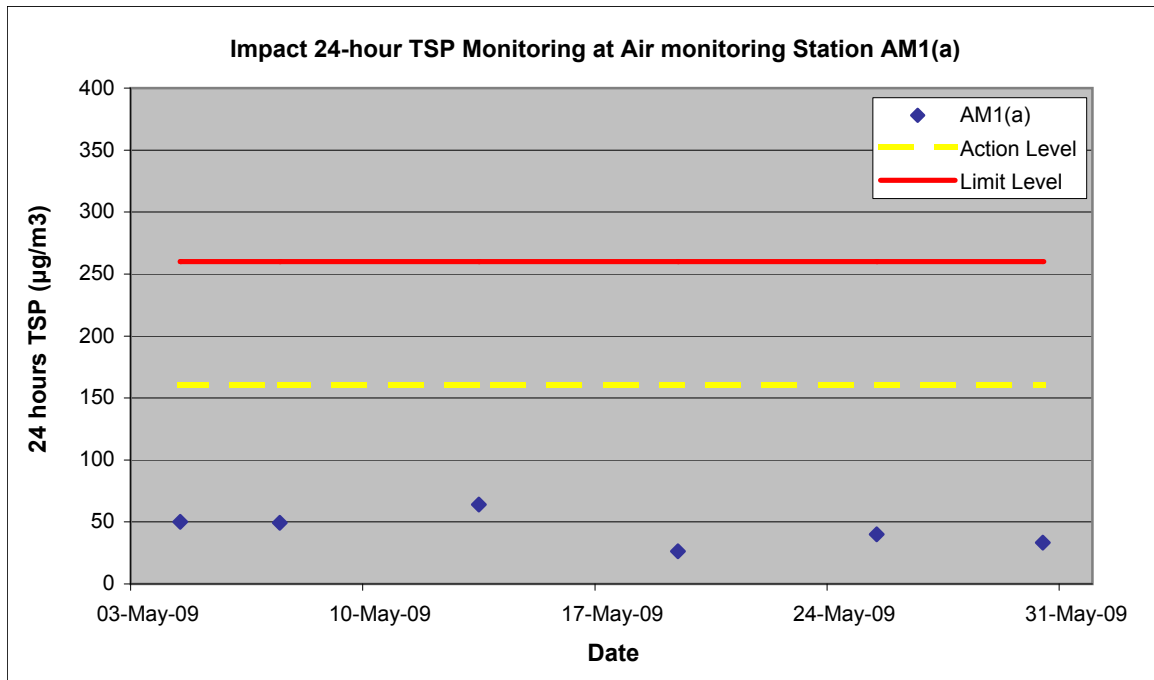

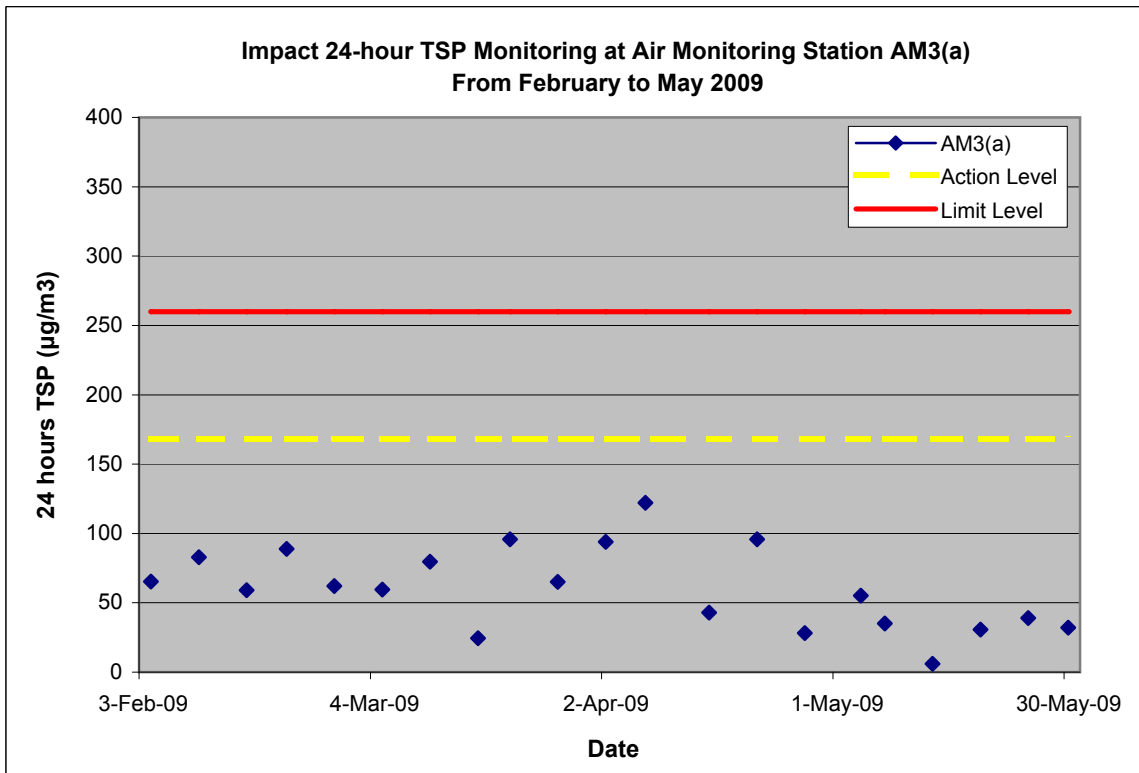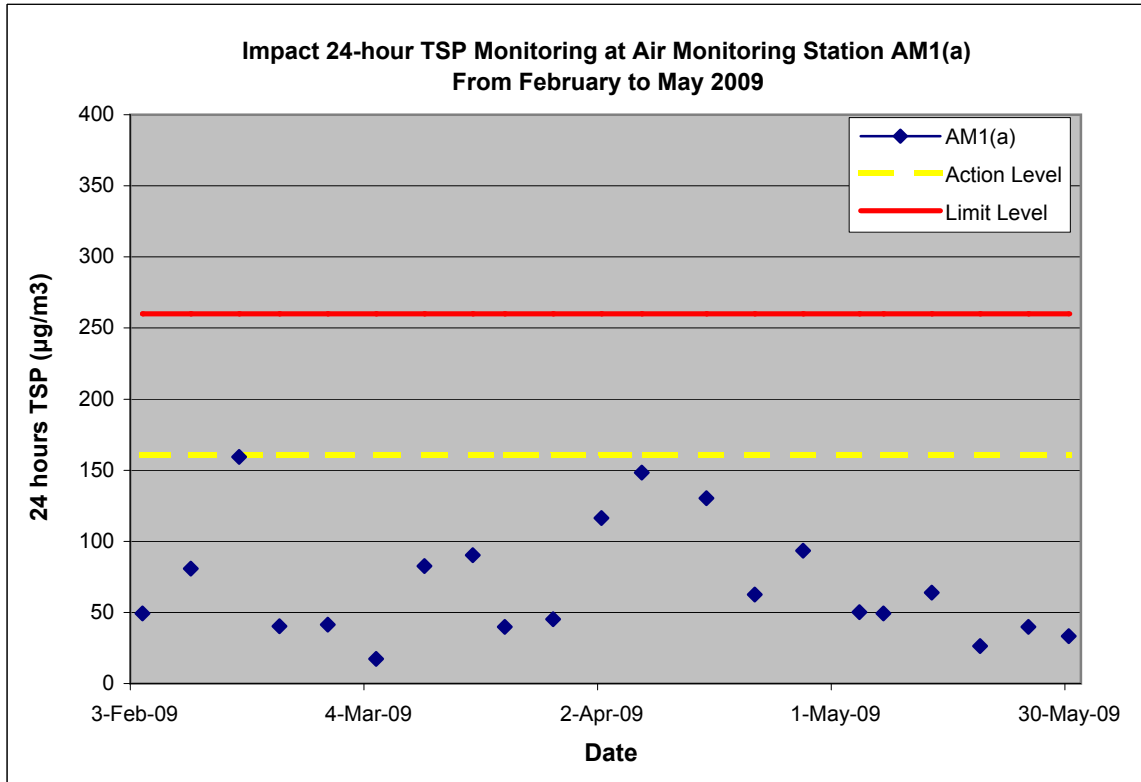


Appendix D


Wind Data

Wind Monitoring Data – Wind Speed during Air Quality Monitoring in May 2009


(公里/小時) (於香港時間 2009 年 5 月 4 日 23 時 50 分更新) (Updated at 23:50H on 4 May 2009) (km/h)

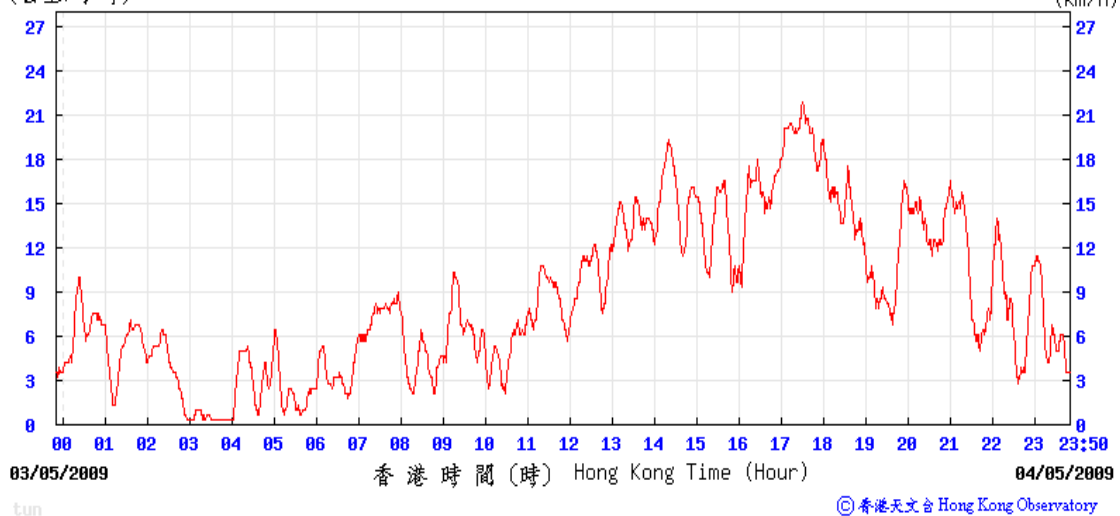


(公里/小時) (於香港時間 2009 年 5 月 6 日 23 時 50 分更新) (Updated at 23:50H on 6 May 2009) (km/h)

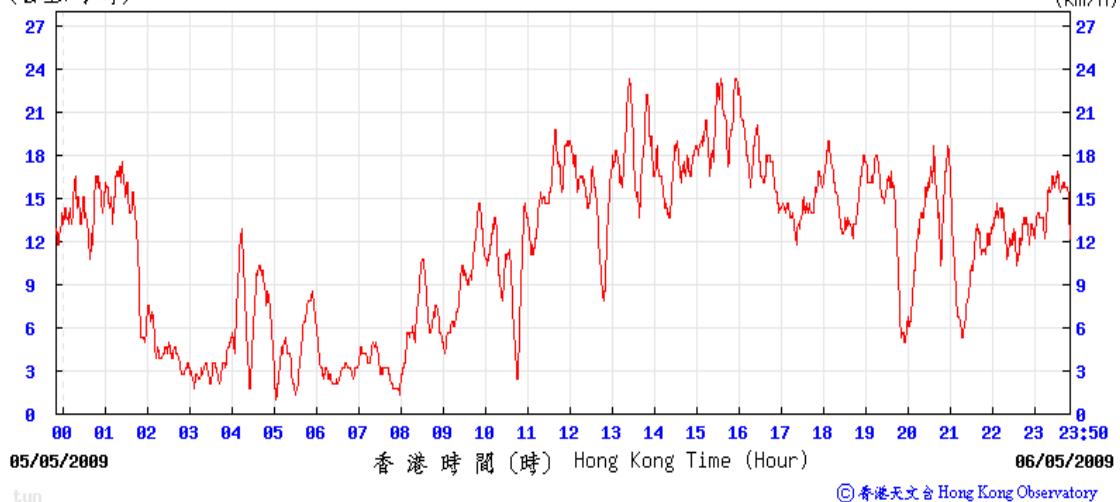


(公里/小時) (於香港時間 2009 年 5 月 7 日 23 時 50 分更新) (Updated at 23:50H on 7 May 2009) (km/h)

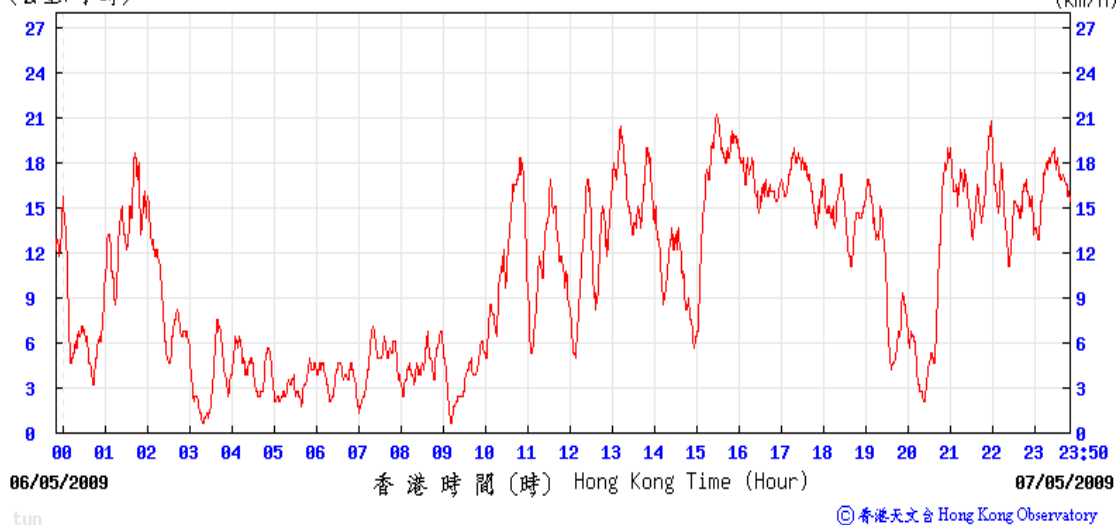


(公里/小時) (於香港時間 2009 年 5 月 12 日 23 時 50 分更新) (Updated at 23:50H on 12 May 2009) (km/h)

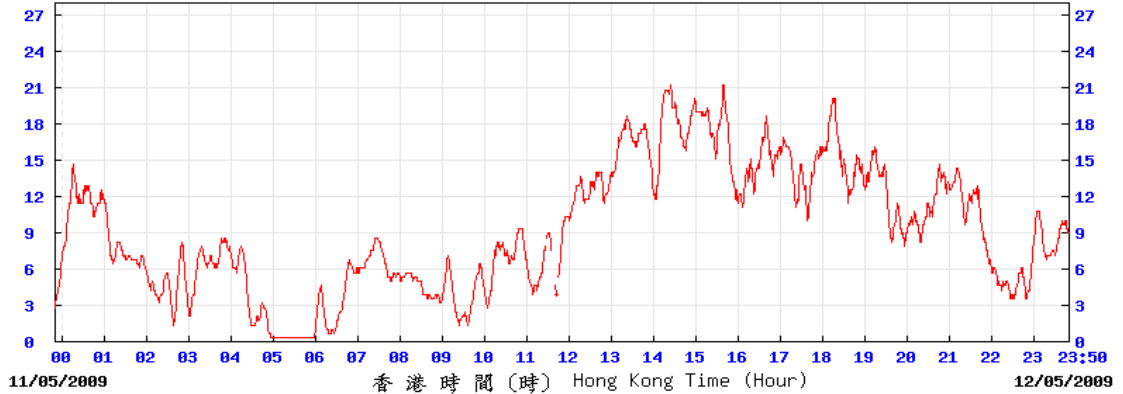


(公里/小時) (於香港時間 2009 年 5 月 13 日 23 時 50 分更新) (Updated at 23:50H on 13 May 2009) (km/h)




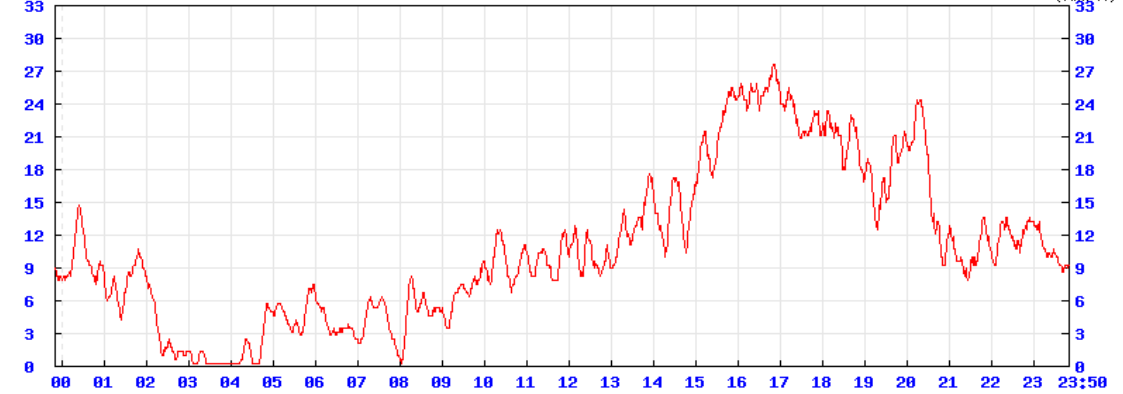


(公里/小時) (於香港時間 2009 年 5 月 18 日 23 時 50 分更新) (Updated at 23:50H on 18 May 2009) (km/h)



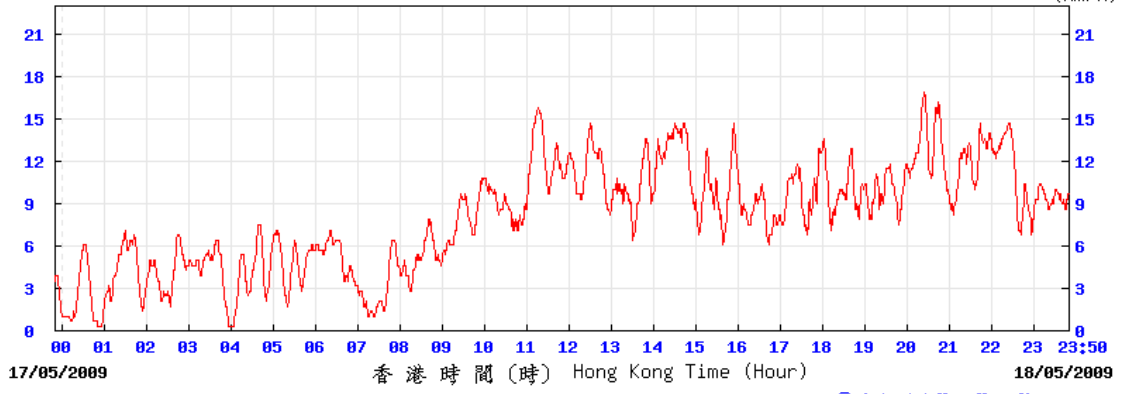






(公里/小時) (於香港時間 2009 年 5 月 19 日 23 時 50 分更新) (Updated at 23:50H on 19 May 2009) (km/h)




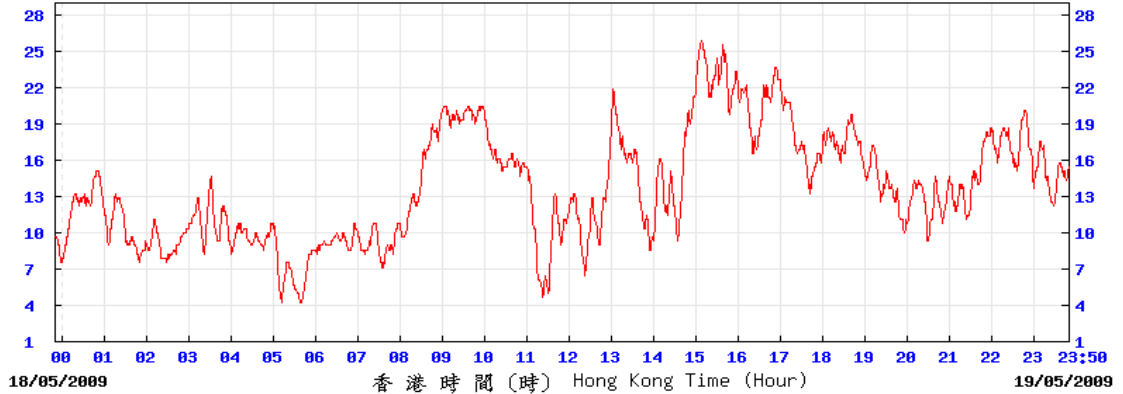


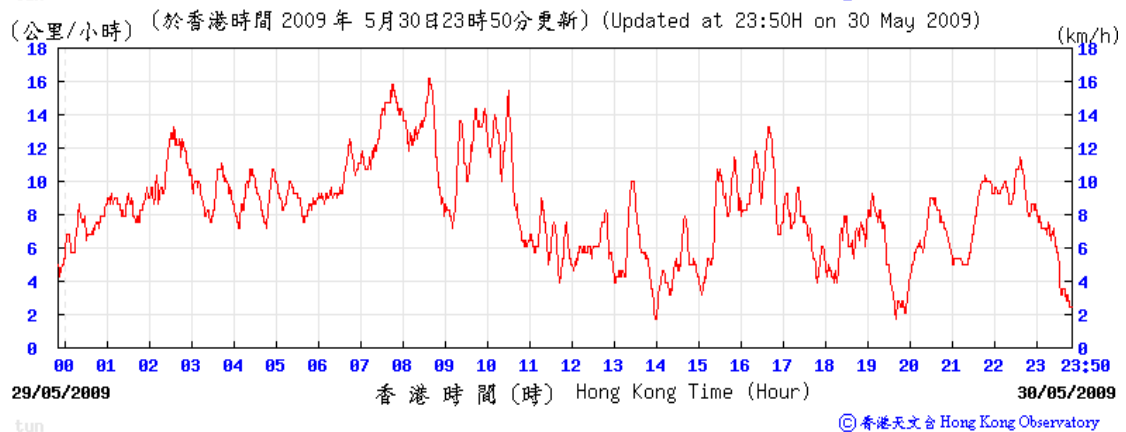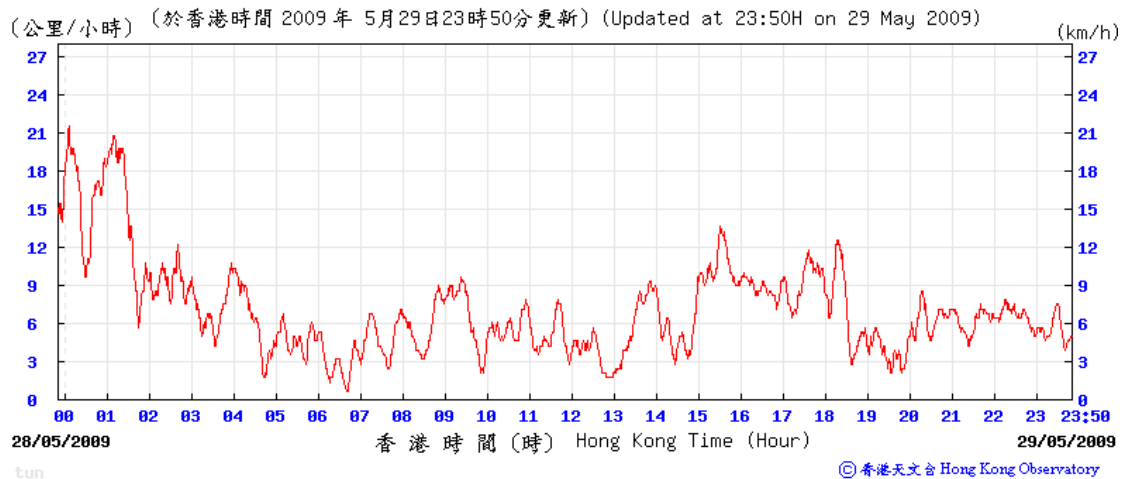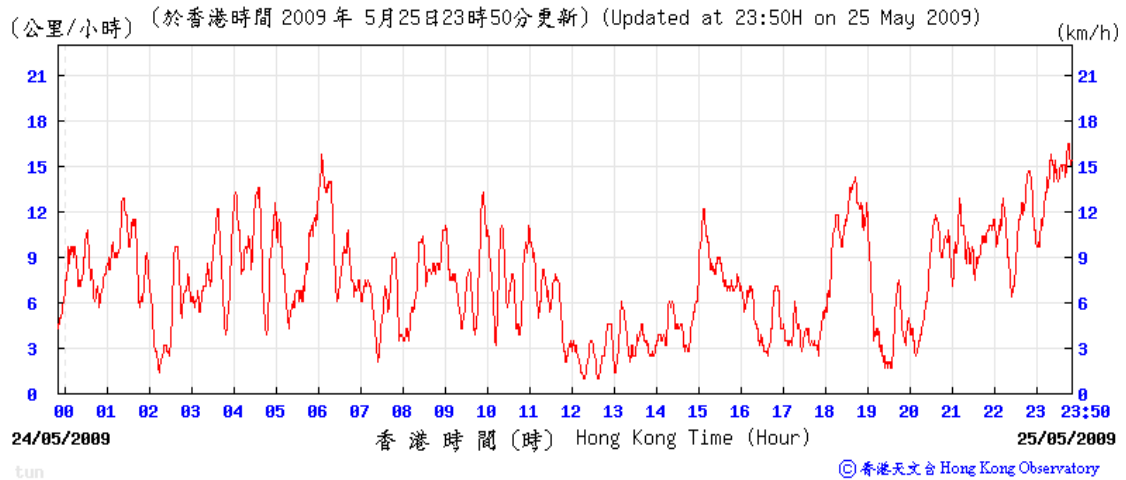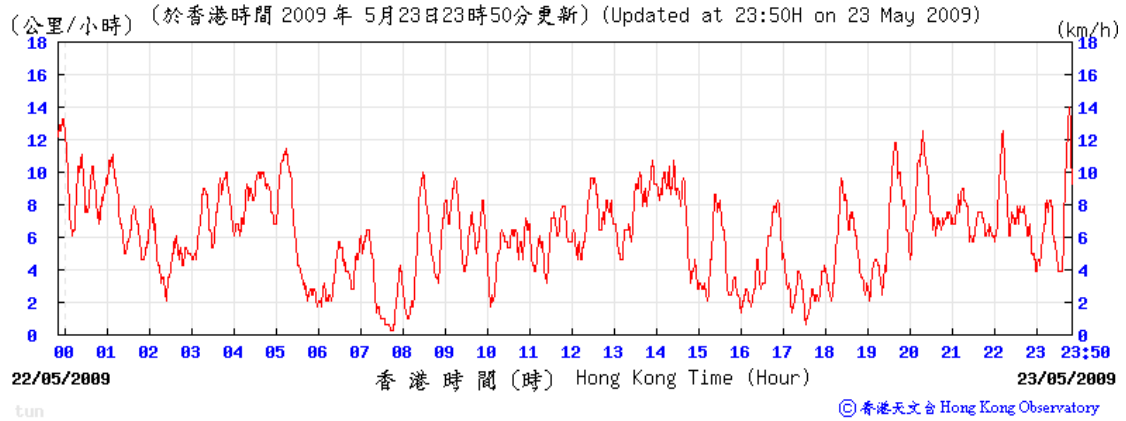

Wind Monitoring Data – Wind Direction during Air Quality Monitoring in May 2009

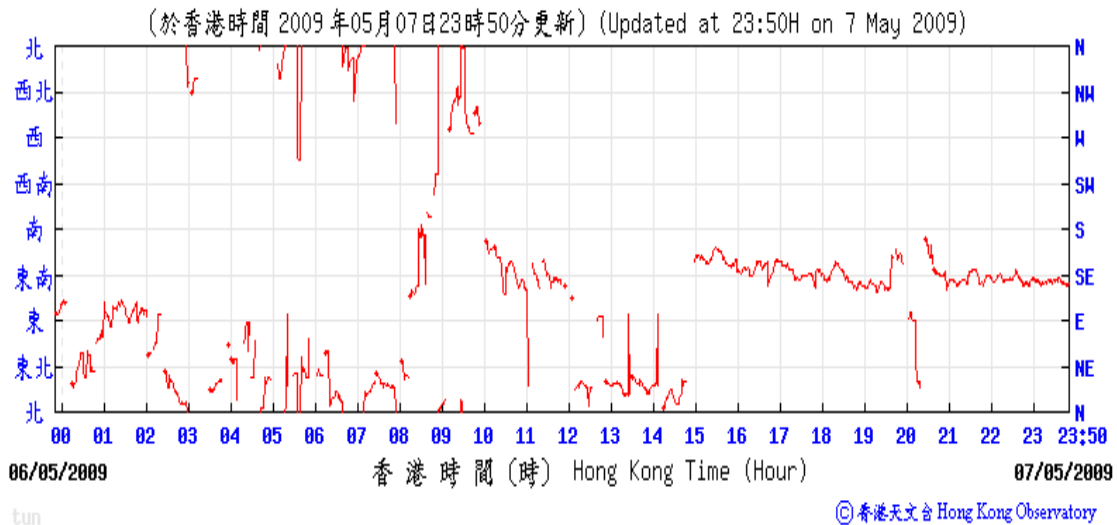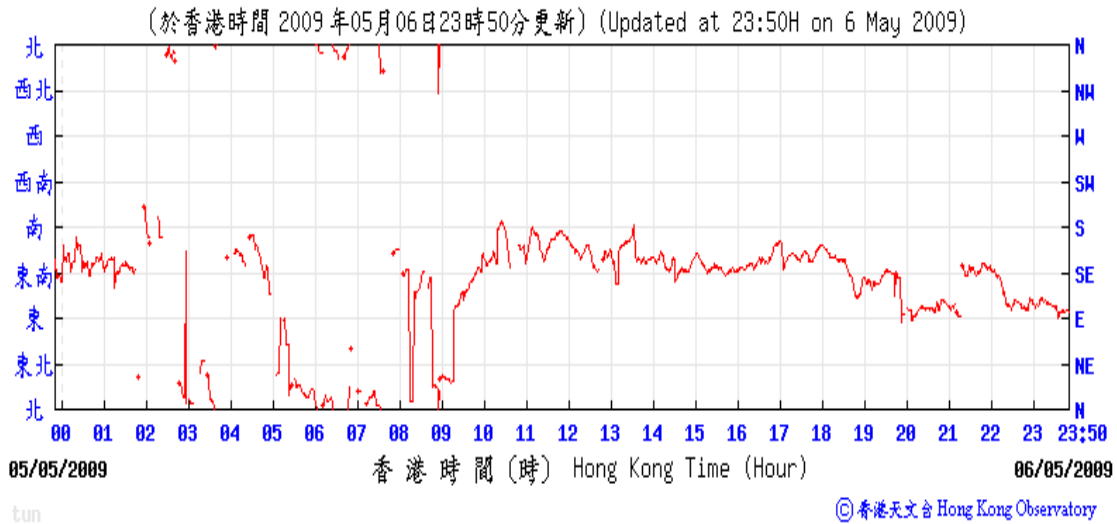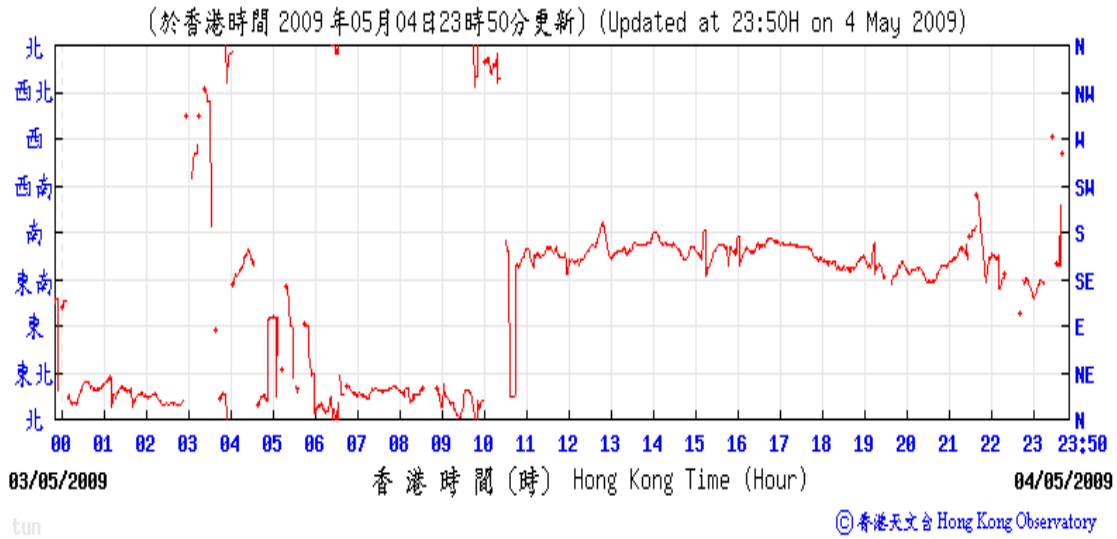

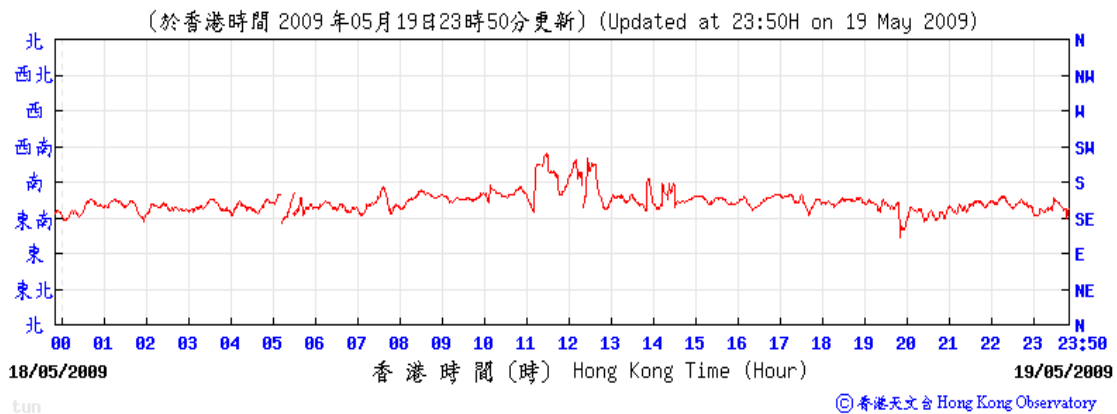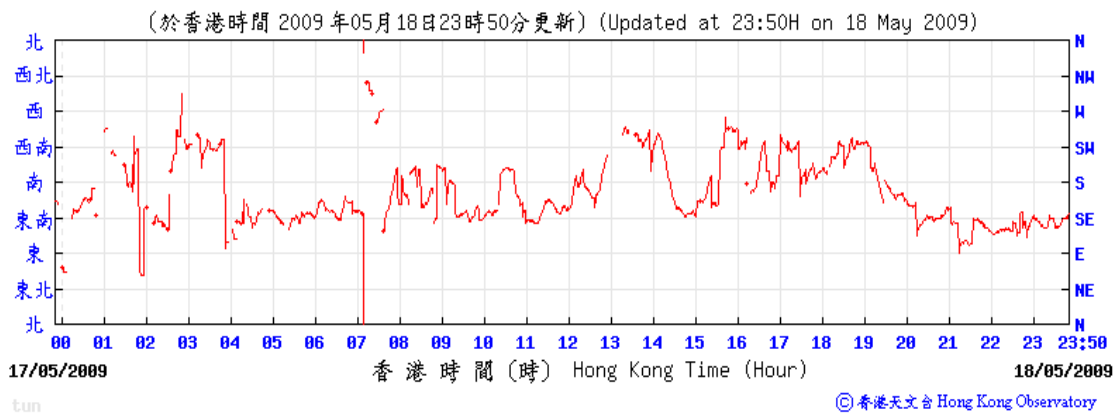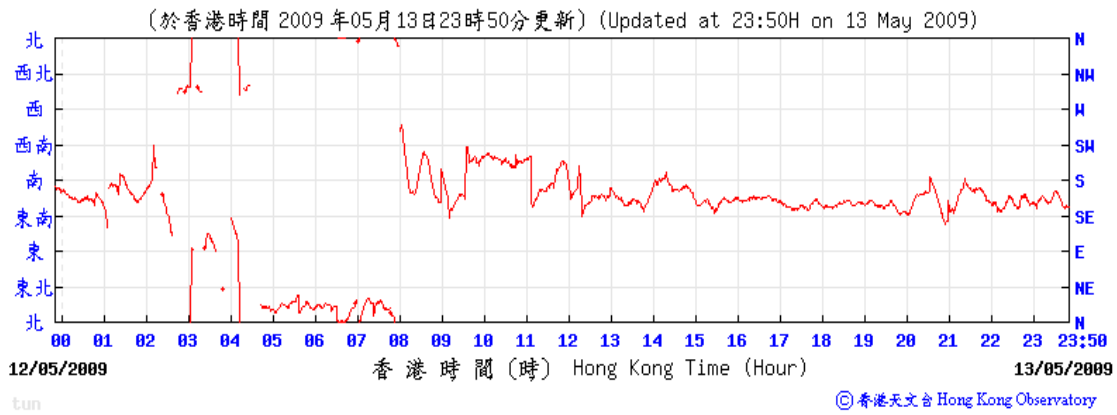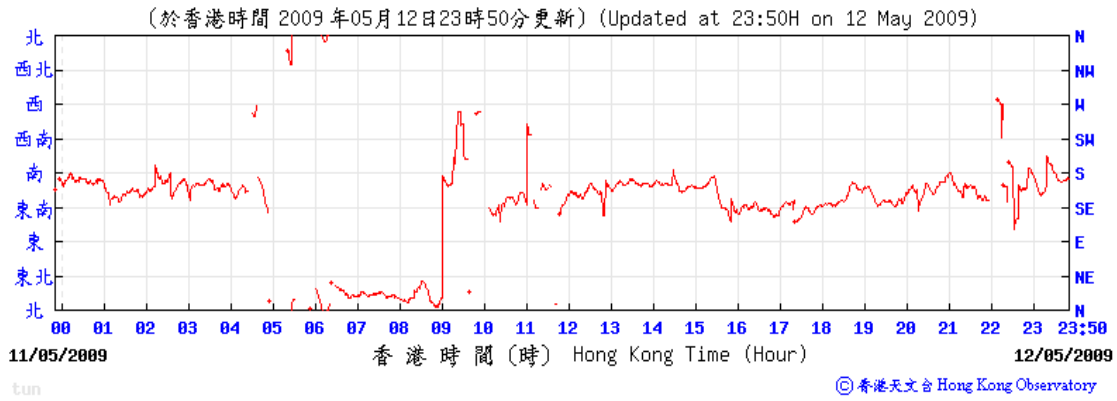

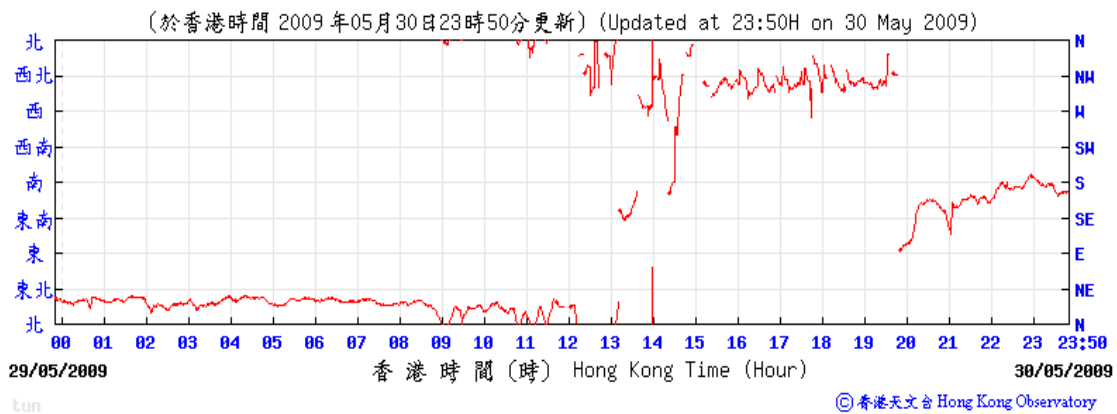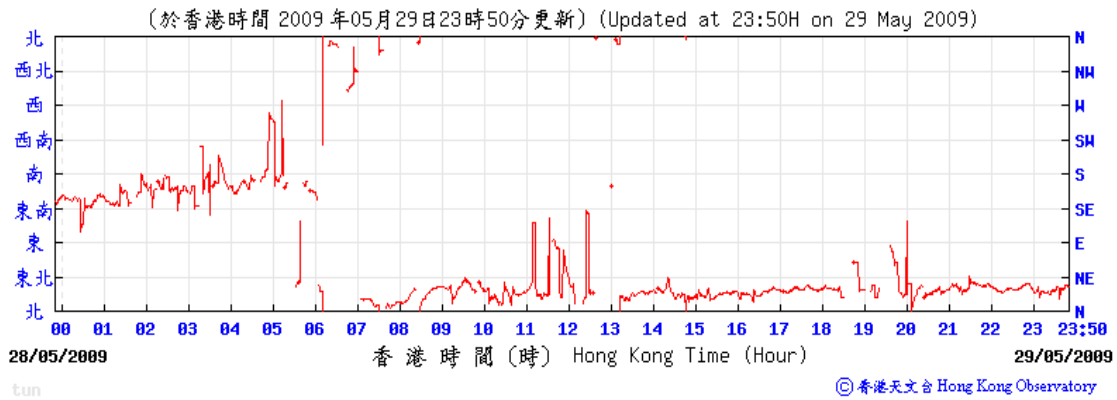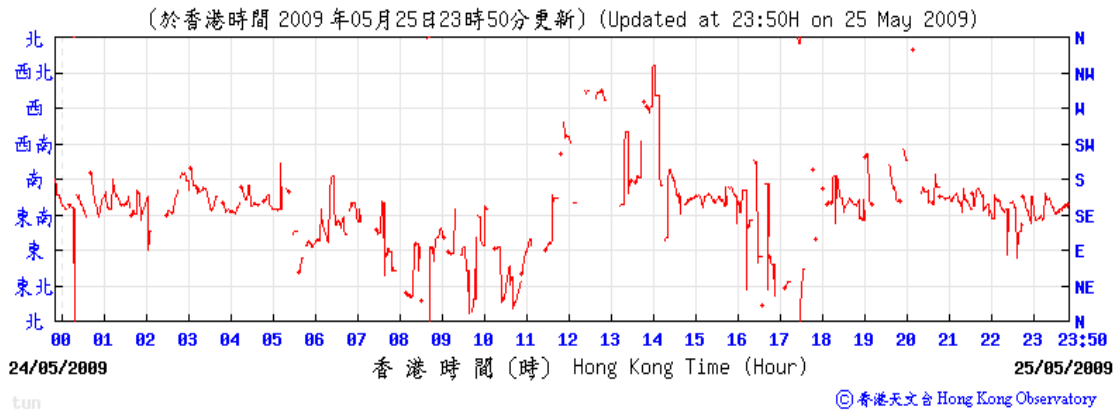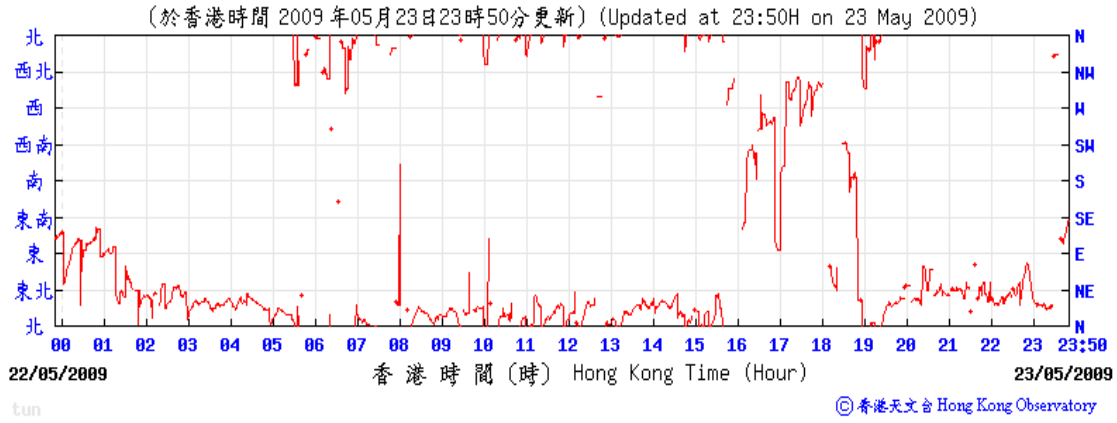

Appendix E

**Calibration Certificate
of Sound Level Meter
and Acoustical
Calibrator**

CERTIFICATE OF CALIBRATION

Issued by: Brüel & Kjær UK Ltd.

Date of Issue: 01 FEB 2007 Certificate Number: 15784



0174

Brüel & Kjær

Bedford House, Rutherford Close, Stevenage.
Hertfordshire. SG1 2ND
Telephone: 01438 739100 Fax.: 01438 739199
E-Mail : ukservice@bksv.com

Page 1 of 4 pages
Approved signatory
Name: A.M. HAMM
Signature:

CALIBRATION OF MULTI FREQUENCY CALIBRATOR TYPE 4226 ("Free Field and Random" version)

Client: ARUP ACOUSTICS
PARKIN HOUSE
8 ST. THOMAS STREET
WINCHESTER SO23 9HE

Calibrator Type 4226, S/No: 1531372
With Coupler UA0915, S/No: 1531372
Client Inventory Number: -
Manufacturer: Brüel & Kjær
Equipment Received on: 23 JAN 2007
Calibration Date: 01 FEB 2007
Brüel & Kjær Reference No: 1-97267724

Measurement Method

The Calibration was performed to Laboratory Procedure TWI-103.

Sound pressure level in the 1/2 inch coupler of the calibrator was measured with a laboratory grade condenser microphone Type 4180, used as a working standard, calibrated by the National Physical Laboratory.

This certificate is issued in accordance with the laboratory accreditation requirements of the United Kingdom Accreditation Service. It provides traceability of measurement to recognised national standards, and to units of measurement realised at the National Physical Laboratory or other recognised national standards laboratories. This certificate may not be reproduced other than in full, except with the prior written approval of the issuing laboratory.

CERTIFICATE OF CALIBRATION

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

15784

Page 2 of 4 pages

The measured sound pressure was compared with that generated in the coupler of a working standard pistonphone calibrated by the National Physical Laboratory whose output was cross checked against a reference standard pistonphone, also calibrated by the National Physical Laboratory, using the same microphone and at the same ambient conditions. Appropriate corrections for atmospheric pressure conditions during calibration and for the measurement frequency and level response were taken into account.

Sound pressure level results are the mean of 5 measurements.

Results apply directly to the following settings on the calibrator, pressure, linear, calibration, 94dB, microphone group a, b, c.

Results for frequency and distortion are the result of a single measurement.

Results for 104 and 114dB are only at 125Hz, 1kHz and 8kHz, compared with the output at 94dB.

Calibration results apply at ambient conditions during the process of calibration.

Calibrations marked (Not UKAS Accredited) in this certificate have been included for completeness.

CALIBRATION RESULTS

4226 Settings: Linear, Pressure, 94dB, Microphone Group c.

Frequency Setting Hz	Sound Pressure Level in dB re 20 μ Pa	Frequency Hz (Not UKAS Accredited)	Distortion % (Not UKAS Accredited)
31.5	94.13	31.63	0.5
63	94.07	63.13	0.2
125	94.04	125.9	0.2
250	94.02	251.3	0.2
500	94.00	502.5	0.2
1k	94.04	1.005 k	0.2
2k	94.02	1.979 k	0.4
4k	94.07	3.957 k	0.7
8k	94.16	7.915 k	0.3
12.5k	94.08	12.66 k	0.2

CERTIFICATE OF CALIBRATION

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

15784

Page 3 of 4 pages

Expanded uncertainty of calibration:

Sound Pressure Level: ± 0.15 dB from 31.5 Hz to 2 kHz,
 ± 0.20 dB at 4 kHz and 8 kHz,
 ± 0.25 dB at 12.5 kHz
Frequency: ± 1 last significant digit reported.
Distortion: $\pm 0.3\%$ distortion.

The reported expanded uncertainty is based on a standard uncertainty multiplied by a coverage factor $k=2$, providing a level of confidence of approximately 95%. The uncertainty evaluation has been carried out in accordance with UKAS requirements.

ADDITIONAL TESTS

Sound Pressure Levels at Settings of 94, 104 and 114 dB

Frequency	Difference 104-94dB	Difference 114-94dB
125 Hz	9.99	19.97
1kHz	10.00	19.98
8kHz	9.96	19.93

Result of a single measurement, expanded uncertainty ± 0.15 dB

Inverted "A" Weighting, Readings Relative to 1kHz in dB

Frequency Hz	31.5	63	125	250	500	1 k	2 k	4 k	8 k	12.5 k
Target Value	+39.4	+26.2	+16.1	+8.6	+3.2	0	-1.2	-1.0	+1.1	+4.3
Reading	39.6	26.2	16.1	8.6	3.2	0.0	-1.2	-1.0	1.2	4.3

Target values according to BS EN 60651 - 1994 - results of a single measurement, values rounded to 0.1 dB, expanded uncertainty ± 0.3 dB.

CERTIFICATE OF CALIBRATION

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

15784

Page 4 of 4 pages

Free Field and Random settings

Freq. Hz	Free Field Setting						Random	
	Microphone Group a		Microphone Group b		Microphone Group c		Microphone Group b	
	Target Value dB	Reading dB	Target Value dB	Reading dB	Target Value dB	Reading dB	Target Value dB	Reading dB
250	0	0.00	0	0.00	0	0.00	0	0.00
500	0	0.00	0	0.00	0	0.00	0	0.00
1k	+0.15	0.15	+0.20	0.19	+0.10	0.10	+0.05	0.03
2k	+0.50	0.49	+0.45	0.44	+0.35	0.34	+0.10	0.09
4k	+1.35	1.34	+1.05	1.04	+0.95	0.93	+0.15	0.13
8k	+4.50	4.47	+2.80	2.78	+2.60	2.58	+0.40	0.38
12.5k	+7.35	7.29	+5.60	5.54	+5.05	5.00	+1.50	1.48

Target values as specified in the manufacturer's manual, result of a single measurement, expanded uncertainty ± 0.2 dB.

Ambient conditions during calibration were:

Atmospheric Pressure 101.7 kPa
Temperature 23 °C
Relative Humidity 47 %

Checked by:



Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong, Kowloon
HONG KONG

AAc Certificate No. 2007001

Fax: +852 2268 3950

Tel: +852 2268 3216

CERTIFICATE OF CONFORMITY

<u>Description of Test Instrument</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjaer 4231Acoustic Calibrator	4231	2314016

Date of Test: 01 September 2007

Carried out by: Raymond Liu

Approved by: William Ng

Signature: *Raymond*

Signature: *William Ng*

Ambient Conditions During Test	
Atmospheric Pressure:	1KPa
Air Temperature:	21°C
Relative Humidity:	58%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

<u>Description of Reference Calibrator</u>	<u>Type No</u>	<u>Serial No</u>
Brüel & Kjær Multi Frequency Calibrator	4226	1531372
Brüel & Kjær Coupler	UA0915	1531372
Certificate of Calibration Serial No.	15784	
By Brüel & Kjær (UK) Ltd Calibration Date:	01 February 2007	
NAMAS Accredited Calibration Laboratory No.	0174	

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

Footnote:

CERTIFICATE OF CALIBRATION

Certificate No. : 2KS081201-3

Page 1 of 2

Calibration of :

Description :	Sound Level Meter	,	Microphone
Manufacture :	Brüel & Kjær		
Type No. :	2238	,	4188
Serial No. :	2562763	,	2658599

Client :

Ove Arup & Partners HK Ltd
Level 5 Festival Walk
80 Tat Chee Avenue
Kowloon Tong
Kowloon

Calibration Conditions :

Air Temperature :	23	°C
Air Pressure :	101.3	kPa
Relative Humidity :	62	%

Test Specifications :

The Sound Level Meter has been calibrated in accordance with the requirements as specified in IEC 60651 and IEC 60804 type 1, and vendor specific procedures.

The measurements has been performed with the assistance of :
Brüel & Kjær's Sound Level Meter Calibration System B&K 9600 CAL2236, Ver.03.11.1995
The standard(s) and instrument(s) used in the calibration are traceable to international standard and are calibrated on a schedule which is adjusted to maintain the required accuracy level.

Test Result :


A list of the performed (sub) tests is stated on page 2 of this certificate. Actual Measurement are documented on worksheet.

Date of Calibration : 03 December, 2008

Certificate issued : 03 December, 2008

Calibrated By :

Approved Signatory :


Dai Bin
Jacky Leung

Reproduction of the complete certificate is allowed. Parts of the certificate may only be reproduced after written permission.

CERTIFICATE OF CALIBRATION

Certificate No. : 2KS081201-3

Page 2 of 2

Results :

List of performed (sub) test with test status:

“OK” Means the result of the (sub)test is Inside the tolerances stated in the test specifications.

“ - ” Means the result of the (sub)test is Outside these tolerances.

Test :	Subtest :	Status :
Noise	A	OK
Noise	C	OK
Noise	Lin	OK
Frequency Weighting	A	OK
Frequency Weighting	C	OK
Frequency Weighting	Lin	OK
Level Range Control	4000 Hz	OK
Linearity Range	SPL 10dB 4000 Hz	OK
Linearity Range	SPL 1dB 1000 Hz	OK
RMS Detector	CF 3	OK
RMS Detector	CF 5	OK
RMS Detector	CF 10	OK
RMS Detector	Symmetry	OK
Time Weighting	Difference in Indication	OK
Time Weighting	Single Burst FAST	OK
Time Weighting	Single Burst SLOW	OK
Time Weighting	Single Burst IMPULSE	OK
Time Weighting	Repetitive Burst	OK
Time Weighting	Peak	OK
Time Averaging		OK
Pulse Range		OK
Overload	SPL	OK
Overload	SEL	OK
Acoustic Response	A	OK
Acoustic Response	Lin	OK

Calibration Equipment :

Brüel & Kjær's Sound Level Meter Calibration System B&K 9600 CAL2236, Ver.03.11.1995

Description :	Make & Model :	Serial No. :	Last Cal. Date :	Traceable to:
Digital Multi-meter	Datron 1281	27361	13 Oct, 2008	HKSCS (HOKLAS)
Sine/Noise Generator	B&K 1049	1314978	Test	B&K Conformance
Test Waveform Generator	B&K 5918	1482949	Test	B&K Conformance
Acoustical Calibrator	B&K 4226	1551627	08 May, 2008	NPL via B&K

Calibrated By : *Dan Børn*
Date : 03 December, 2008

Checked By : *Jens*
Date : 03 December, 2008


Appendix F

**Impact Noise
Monitoring Results**


**The Church of Christ in China Tam Lee Lai Fun Memorial Secondary School, TLLF(a)
 Day-time Noise Monitoring Data**

Note (*): Façade correction is included.

Date	Start Time	L _{eq} (5-min), dB(A)	L _{eq} (30-min), dB(A)*	L10 (5min), dB(A)	L10 (5-min), dB(A)*	L ₉₀ (5min), dB(A)	L ₉₀ (5min), dB(A)*
6-May-09	1:10 PM	65	69	69	72	64	67
	1:15 PM	66		69		64	
	1:20 PM	66		69		64	
	1:25 PM	67		70		64	
	1:30 PM	67		69		63	
	1:35 PM	67		69		64	
12-May-09	11:35 AM	66	69	71	74	63	66
	11:40 AM	66		72		62	
	11:45 AM	66		71		62	
	11:50 AM	66		71		64	
	11:55 AM	67		72		64	
	12:00 PM	67		72		64	
18-May-09	9:20 AM	69	73	73	76	64	68
	9:25 AM	69		72		63	
	9:30 AM	70		73		65	
	9:35 AM	70		73		65	
	9:40 AM	71		74		66	
	9:45 AM	71		73		65	
18-May-09	10:05 AM	69	72	72	75	66	68
	10:10 AM	69		72		65	
	10:15 AM	69		72		66	
	10:20 AM	69		72		65	
	10:25 AM	69		72		66	
	10:30 AM	69		72		65	
29-May-09	9:05 AM	70	73	72	75	66	69
	9:10 AM	69		72		67	
	9:15 AM	70		73		67	
	9:20 AM	70		73		67	
	9:25 AM	71		73		67	
	9:30 AM	71		73		66	
29-May-09	10:05 AM	69	72	72	75	66	69
	10:10 AM	69		72		66	
	10:15 AM	69		72		66	
	10:15 AM	69		73		67	
	10:20 AM	68		72		66	
	10:25 AM	68		71		65	

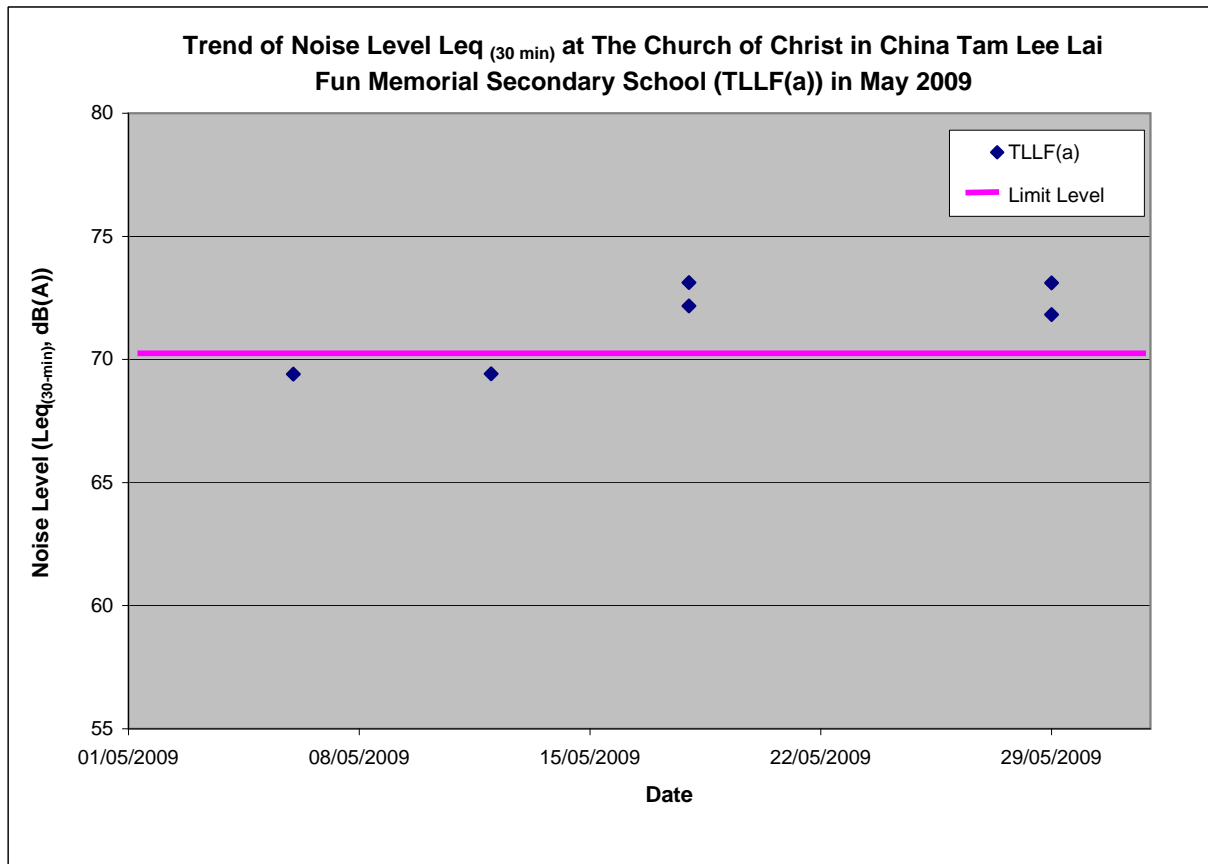


Notes:
Noise results on 18 and 29 May 2009 are not project-related exceedance

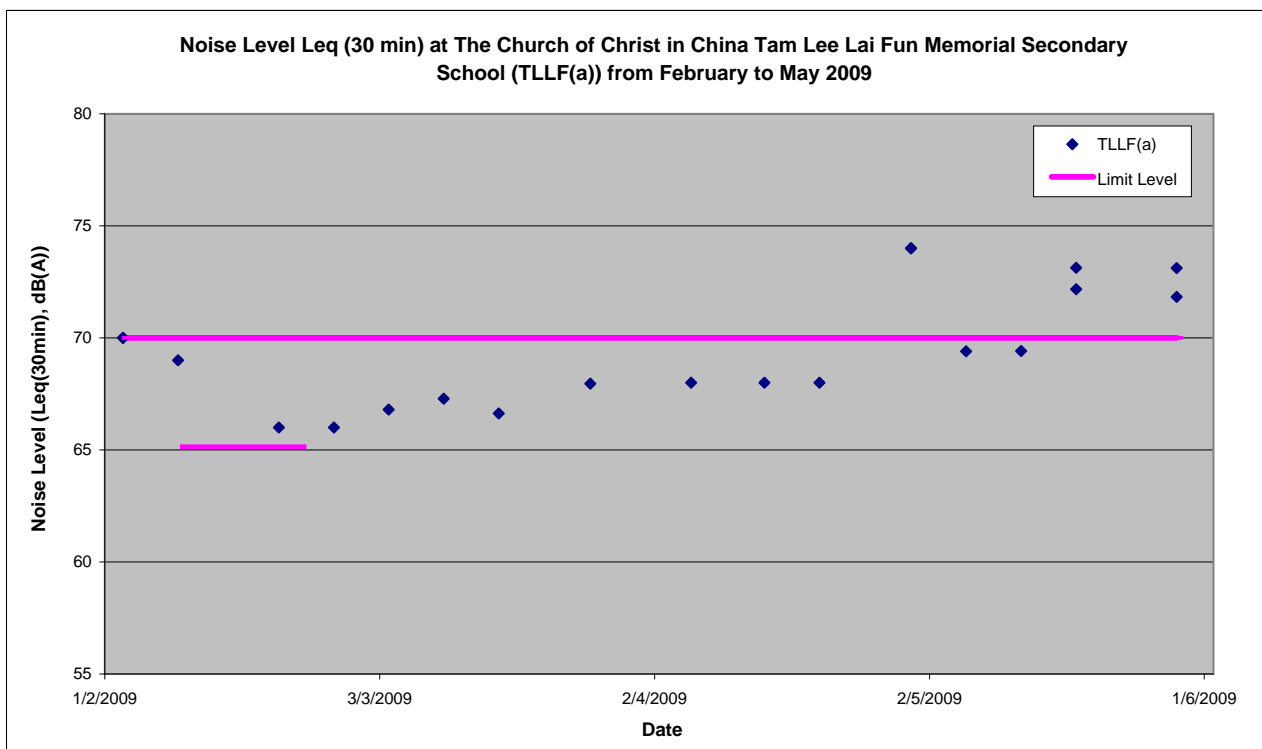

Notes:
All noise results exceeding limit level were not project-related.

Appendix G

**Locations of the
Transplanted Tress**

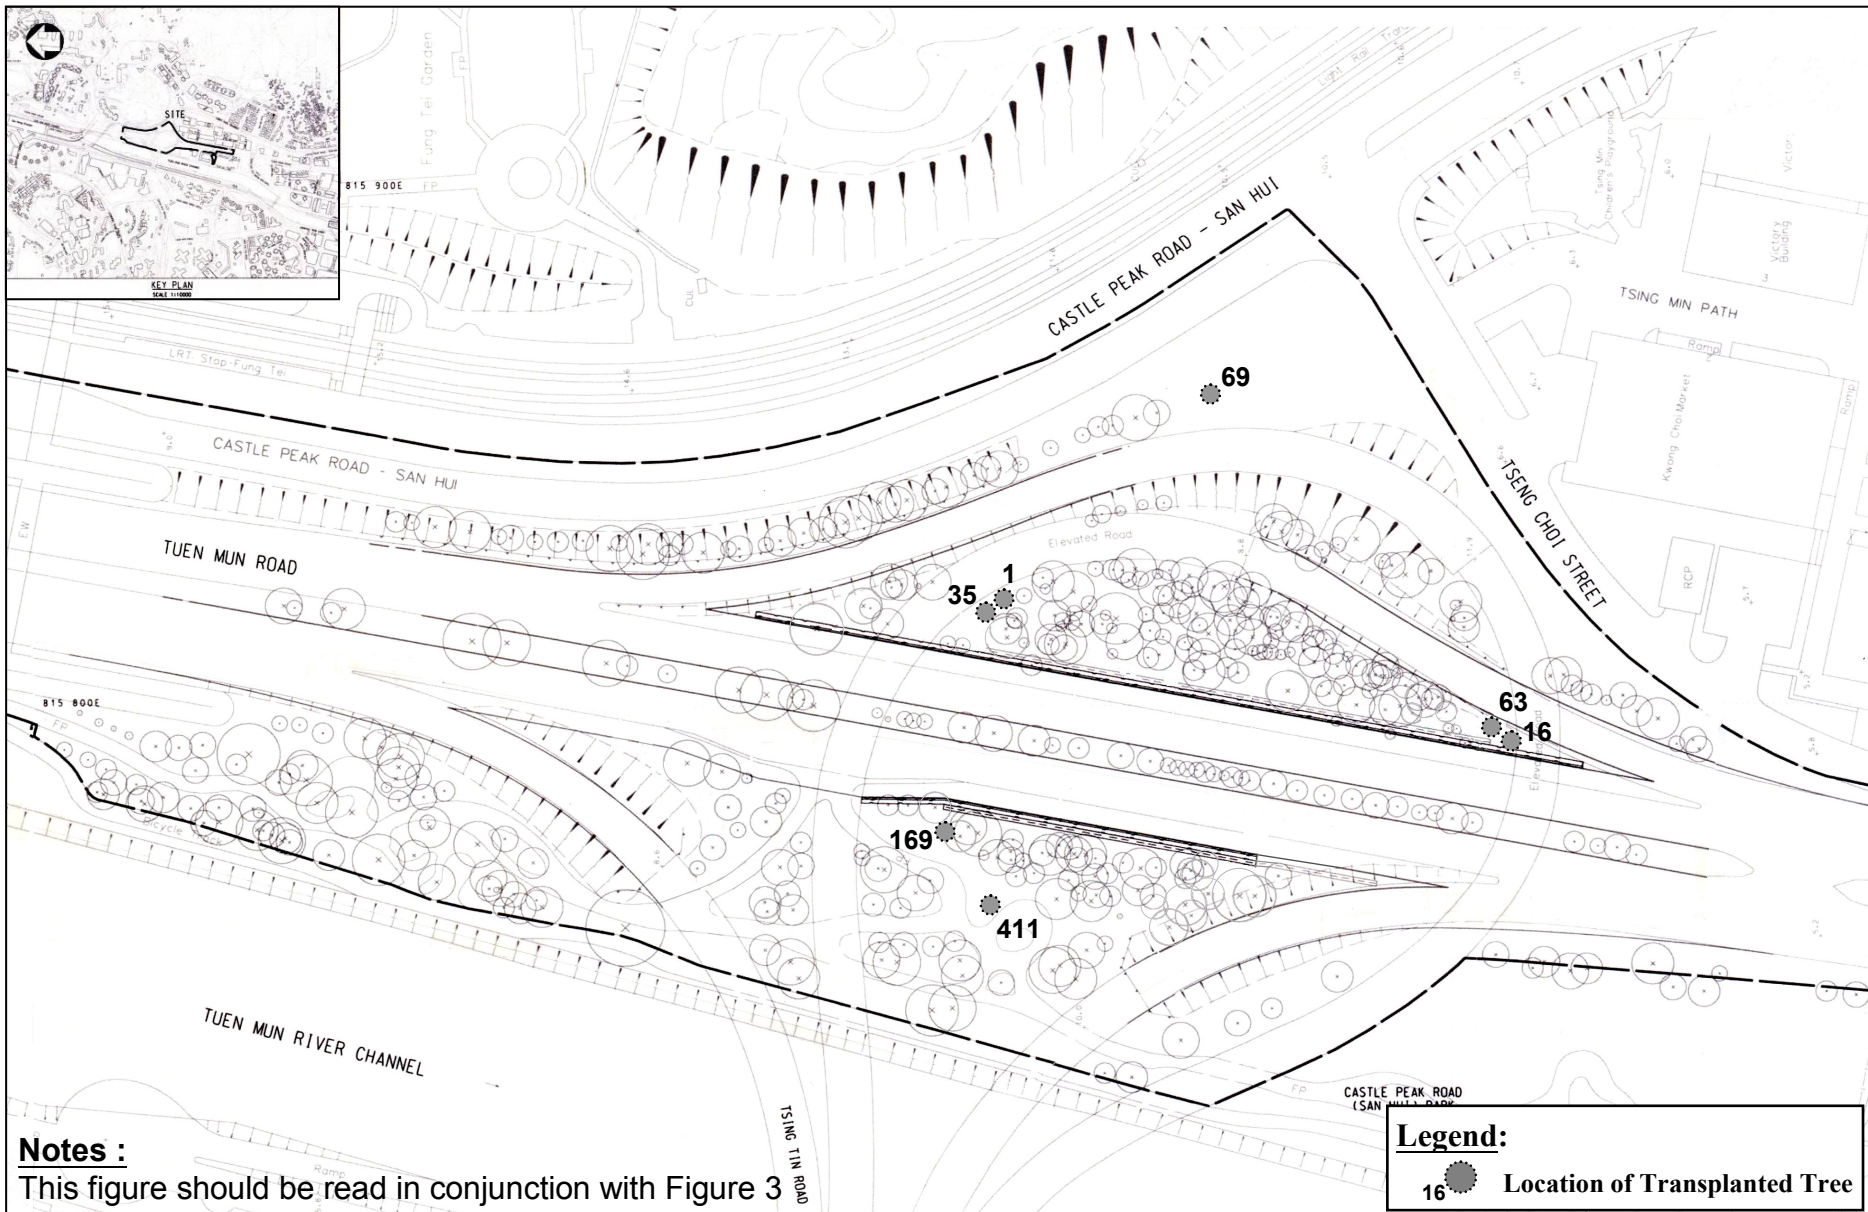

**Widening of Tuen Mun Road at Tsing Tin Interchange
- Locations of Transplanted Trees**

Figure 4
Environmental Permit No. :
EP-302/2008/B



Appendix H

**Updated Summary of
Environmental
Mitigation
Implementation
Schedule**

Summary of Environmental Mitigation Implementation Schedule

EIA Ref #	Mitigation Measures	Location / Timing	Status *
Air Quality Control			
S3.8.1	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. <ul style="list-style-type: none"> • skip hoist for material transport should be totally enclosed by impervious sheeting • every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site • the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores • where a site boundary adjoins a road, streets or other accessible to the public, hording of not less than 2.4m high from ground level should be provided along the entire length except for a site entrance or exit • every stack of more than 20 bags of cement should be covered entirely by impervious sheeting places in an area sheltered on the top and the 3 sides • all dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet • the height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading • the load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle • instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise 	Work site / during construction	✓ ✓ ✓ ✓ N/A ✓ N/A N/A N/A
Noise Control			
S4.8.1	Use of quiet powered mechanical equipment	Work Sites / During Construction	N/A
S4.8.5 – S4.8.6	Road paving - Adoption of quiet PMEs, movable noise barrier and scheduling of PMEs during normal teaching period, only one PME to be operated and the work area not less than 22m from NSR TLLF or cease operation of PMEs if work area less than 30m from NSR TLLF during examination period. The barrier material shall have a surface mass of	Work Site for road paving, road marking and construction of noise barrier in the vicinity of	✓

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	Mitigation Measures	Location / Timing	Status *
	not less than 14 kg/m ² on skid footing with 25mm thick internal sound absorptive lining.	NSR TLFF (The Church of Christ in China Tam Lee Lai Fun Memorial Secondary School) / During Construction	
S4.8.5 & S4.8.7	Road marking - Adoption of quiet PMEs and movable noise barrier during normal teaching period and examination period. The work area should be located not less than 18m from NSR TLLF during examination period. The barrier material shall have a surface mass of not less than 14 kg/m ² on skid footing with 25mm thick internal sound absorptive lining.	Work Site for road marking in the vicinity of NSR TLFF / During Construction	N/A
S4.8.5 & S4.8.8	Construction of noise barrier - Adoption of quiet PMEs and movable noise barrier during examination period, piling operation for construction of noise barrier would also be ceased during examination period. The barrier material shall have a surface mass of not less than 14 kg/m ² on skid footing with 25mm thick internal sound absorptive lining.	Work Site for construction of noise barrier in the vicinity of NSR TLFF / During Construction	N/A
S4.9.2	<p><i>Good Site Practice:</i></p> <ul style="list-style-type: none"> • Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program. • Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program. • Mobile plant, if any, should be sited as far away from NSRs as possible. • Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum. • Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. • Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities. • Scheduling the noisy work to be conducted in non-school hours or long holiday such as summer vacation as possible. 	Work Sites / During Construction	<p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>N/O</p> <p>N/A</p> <p>N/A</p>
Water Quality Control			

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	Mitigation Measures	Location / Timing	Status *
S5.7.2	<p><i>Measures for Tuen Mun River Channel</i></p> <ul style="list-style-type: none"> • Site runoff would be directed towards regularly cleaned and maintained sand traps, silt traps and where appropriate. • Oil/grease separators to minimise risk of sedimentation and pollution to the River Channel. • Debris and rubbish generated on-site would be collected, handled and disposed of properly. • The stockpile or temporary storage area and chemical waste storage area shall be located at least 30m away from Tuen Mun River Channel. 	Work site / During the construction period	<p style="text-align: center;">✓</p> <p style="text-align: center;">N/A</p> <p style="text-align: center;">✓</p> <p style="text-align: center;">✓</p>
S5.7.3	<p><i>Construction Runoff and Drainage</i></p> <p>The site practices outlined in ProPECC PN 1/94 “Construction Site Drainage” shall be implemented including:</p> <ul style="list-style-type: none"> • Sand/silt removal facilities such as sand traps, silt traps or sediment basins shall be provided to remove sand/silt particles from runoff to meet the requirements of the Technical Memorandum standard under the Water Pollution Control Ordinance. The design of silt removal facilities should be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures should be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms. • Water pumped out from foundation excavations should be discharged into silt removal facilities. • Careful programming of the works to minimise surface excavations during the rainy season. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by a tarpaulin or other means. Other measures that need to be implemented before, during, and after rainstorms are summarized in ProPECC PN 1/94. • Exposed soil surface shall be protected by paving as soon as possible to reduce the potential of soil erosion. • Open stockpiles of construction materials on site shall be covered with tarpaulin or similar fabric during rainstorms. 	Work site / During the construction period	<p style="text-align: center;">✓</p> <p style="text-align: center;">✓</p> <p style="text-align: center;">N/A</p> <p style="text-align: center;">N/A</p> <p style="text-align: center;">✓</p>

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	Mitigation Measures	Location / Timing	Status *
S5.7.4 – S5.7.5	<p><i>Sewage from General Construction Activities</i></p> <p>Debris and rubbish generated on-site shall be collected, handled and disposed of properly to avoid entering the nearby nullah and stormwater drains. Stockpiles of cement and other construction material should be kept covered when not being used.</p> <p>Oils and fuels should only be used and stored in designated areas which have pollution prevention facilities. All fuel tanks and storage areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event.</p>	Work site / During the construction period	<p>✓</p> <p>✓</p>
S5.7.6	<p><i>Sewage Effluent</i></p> <p>Temporary sanitary facilities, such as portable toilets, shall be employed on-site. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities.</p>	Work site and adjacent water / During the design and construction period.	✓
Waste Management			
S6.6.1	<p><i>Good Site Practices</i></p> <p>Recommendations for good site practices during the construction activities include:</p> <ul style="list-style-type: none"> • nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; • training of site personnel in proper waste management and chemical waste handling procedures; • provision of sufficient waste disposal points and regular collection for disposal; • appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; • regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and • recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites). 	Work site / During the construction period	<p>N/O</p> <p>✓</p> <p>✓</p> <p>✓</p> <p>✓</p>
S6.6.2	<p><i>Waste Reduction Measures</i></p> <p>Waste reduction is best achieved at the planning and design stage, as well as by</p>	Work site / During planning and design	

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	Mitigation Measures	Location / Timing	Status *
	<p>ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> • segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; • to encourage collection of aluminium cans, PET bottles and paper, separate labelled bins shall be provided to segregate these wastes from other general refuse generated by the work force; • any unused chemicals or those with remaining functional capacity shall be recycled; • use of reusable non-timber formwork to reduce the amount of C&D material. • prior to disposal of C&D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill; • proper storage and site practices to minimise the potential for damage or contamination of construction materials; and • plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. 	stage, and construction stage	<p>N/A</p> <p>N/O</p> <p>N/O</p> <p>N/O</p> <p>N/O</p> <p>N/O</p>
S6.6.4	<p><i>General Refuse</i></p> <p>General refuse should be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material.</p> <p>A collection area should be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind blow' light material.</p>	Work site / During the construction period	<p>✓</p> <p>N/O</p>
S6.6.5	<p><i>Chemical Wastes</i></p> <p>After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals should be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.</p>	Work site / During the construction period	<p>✓</p>

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	Mitigation Measures	Location / Timing	Status *
S6.6.6 & 6.6.7	<p><i>Construction and Demolition Material</i></p> <p>Excavated fill material shall be reused on-site as backfill material as far as possible. The material to be disposed at public fill reception facility shall be free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered to be unsuitable by the Filling Supervisor.</p>	Work site / During the construction period	✓
Hazard to Life			
S8.8.4	<ul style="list-style-type: none"> • The number of workers on site during construction stage should be kept as the level as assessed in this report. • Emergency evacuation procedures should be formulated and Highways Department (HyD) should ensure all workers on site should be familiar with these procedures as well as the route to escape in case of gas release incident occur. Relevant Departments, such as Water Supplies Department and Fire Services Department, should be consulted during the development of Emergency procedures. Diagram showing the escape routes to a safe place should be posted in the site notice boards and at the entrance/exit of site. • The emergency procedures should specify means of providing a rapid and direct warning (e.g. Siren and Flashing Light) to construction workers in the event of chlorine gas release in the Tuen Mun Water Treatment Works (TMWTW). • The construction site officer of HyD should establish a communication channel with the TMWTW operation personnel during construction stage. In case of any hazardous incidents in the treatment works, operation personnel of TMWTW should advise the site officer to evacuate the construction workers. 	Works area/ During construction phase	N/O N/O N/O
S8.8.5	Induction Training should be provided to any staff before working on site at the Tsing Tin Interchange work site.	Works area/ During construction phase	N/O
S8.8.6	Periodic drills should be coordinated and conducted to ensure all construction staffs are familiar with the evacuation procedures. Upon completion of the drills, a review on every step taken should be conducted to identify area of improvement.	Works area/ During construction phase	N/O
Ecology			
S9.7.2	Construction activities would be confined to developed areas of low ecological value, and there would be no direct impact to other habitats within the Assessment Area.	Works area / During construction phase	✓
S9.7.4	To mitigate the noise impacts to habitats and associated wildlife within and adjacent to	Works area / During	✓

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	Mitigation Measures	Location / Timing	Status *
	the proposed works area, quiet mechanical plants and well-maintained plants should be used wherever possible. Noise-emitting construction plant should be installed away from the egress as far as practical. Schedule of construction programme should be carefully planned to avoid noise-generating construction activities with high disturbance impact during the breeding seasons of the ardeids (i.e. mid-March to August).	construction phase	
S9.7.5	<p>Noise barrier should also be implemented to mitigate the noise impact in operation phase. To minimize the bird collision impact, precautionary and bird-friendly approach to noise barrier design should be implemented:</p> <ul style="list-style-type: none"> • The transparent materials of the noise barriers would be non-glaring and not light-reflective. • Noise barrier panels would be with either tinted materials, embedded opaque stripes or superimposed patterns of thin opaque stripes. • Noise barrier would be made visible to birds, such as putting falcon stickers on the transparent panels. 	Works area / during construction phase	<p>N/O</p> <p>N/O</p> <p>N/O</p>
S9.7.7	<p>Standard good site practice measures should be implemented throughout the construction phase. The measures should include:</p> <ul style="list-style-type: none"> • Placement of equipment in designated works areas selected on existing disturbed land. • Construction activities should be restricted to the proposed works area that would be clearly demarcated. • The proposed works area should be reinstated immediately after completion of the works. • Open burning on proposed works sites is illegal, and should be strictly enforced. • Waste skips should be provided to collect general refuse and construction wastes. The wastes should be disposed of timely and properly off-site. • Any soil contamination with fuel leaked from construction plants should be removed off-site. 	Works area / during construction phase	<p>N/A</p> <p>✓</p> <p>N/O</p> <p>✓</p> <p>N/O</p> <p>✓</p>
S9.7.8	To minimize the construction dust impact to the vegetation within and in vicinity of the proposed works area, the following mitigation measures as listed below should be implemented:	Works area / During construction phase	

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

EIA Ref #	Mitigation Measures	Location / Timing	Status *
	<ul style="list-style-type: none"> • Regular watering should be used during the construction stage. • Any aggregate or dusty material storage piles should be completely covered. • Minimum practical height for dropping of excavated material should be applied. 		<p style="text-align: center;">✓ N/O N/O</p>
S9.7.9	<p>To minimize the indirect impacts to the nearby Tuen Mun River Channel, the following measures should be implemented:</p> <ul style="list-style-type: none"> • Any runoff and drainage water with high levels of suspended solids should be prevented from entering the nearby water-bodies. • Site runoff should be directed towards regularly cleaned and maintained silt traps and oil/grease separators to avoid and minimise the risk of sedimentation and pollution of the nearby stream courses and drainage culvert. • The silt and oil/grease separators should be appropriately designed for the local drainage and ground conditions. • Debris and rubbish generated on-site should be collected, handled and disposed of properly. 	Works area / during construction phase	<p style="text-align: center;">✓ ✓ N/O ✓</p>
S9.7.10	Compensatory planting of a ratio not less than 1:1 ratio in terms of quality and quantity should be provided to compensate for the loss of roadside trees due to the construction works.	Works area / during construction phase	<p style="text-align: center;">✓</p>
Landscape and Visual			
Table 10.6	CM1 Topsoil, where identified and practical, should be stripped and stored for re-use in the construction of the soft landscape works.	Work site / During Construction Phase	N/O
Table 10.6	CM2 Existing trees to be retained on site should be carefully protected during construction.	Work site / During Construction Phase	✓
Table 10.6	CM3 Trees unavoidably affected by the works should be transplanted where practical.	Work site / During Construction Phase	✓
Table 10.6	CM4 Compensatory tree planting should be provided to compensate for felled trees.	Work site / During Construction Phase	✓
Table 10.6	CM5 Control of night-time lighting.	Work site / During Construction Phase	✓
Table 10.6	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	N/O

Notes (*): ✓ – Compliance; N/A - Not Applicable; N/O – Not Observed; Rdr – Reminder; Obs – Observation; N/C - Non Compliance

Appendix I

**Monthly Summary
Waste Flow Table**

Name of Department : HyD

Contract No. : HY/2007/14

Monthly Summary Waste Flow Table for 2009 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly					Actual Quantities of C&D Wastes Generated Monthly					
	Total Quantity Generated (in '000m ³)	Hard Rocks and Large Broken Concrete (in '000m ³)	Reused in the Contract (in '000m ³)	Reused in other Projects (in '000m ³)	Disposed as Public Fill (in '000m ³)	Imported Fill (in '000m ³)	Metals (in '000 kg)	Paper/ cardboard packaging (in '000kg)	Plastics (see Note 3) (in '000kg)	Chemical Waste (in '000kg)	Others, e.g. general refuse (in '000m ³)
Jan	0.060	0	0	0	0.060	0	0.002	0.010	0	0.5	0.010
Feb	0.735	0	0	0	0.735	0	0.003	0.010	0	0	0.005
Mar	0.645	0	0	0	0.645	0	0.004	0.015	0	0	0.015
Apr	0.330	0	0	0	0.330	0	0.004	0.015	0	0.5	0.005
May	0.820	0	0	0	0.820	0	0.004	0.012	0	0	0.005
June											
Sub-total											
July											
Aug											
Sept											
Oct											
Nov											
Dec											
Total											

Notes: (1) Not Used.

(2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.

(3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material

Appendix J

**Environmental
Monitoring Programme
for Coming Months**

**Contract No. HY/2007/14 Widening of Tuen Mun Road at Tsing Tin Interchange
Tentative Impact Monitoring Schedule (Jun 2009) Revision 2**

Date	Air Quality		Noise	Landscape & Visual	Weekly Site Inspection
	1-hour TSP	24-hours TSP	L _{Aeq} , 30 min		
1-Jun-09 Mon					
2-Jun-09 Tue					
3-Jun-09 Wed	AM1(a) & AM3(a)		TLLF(a)		SSEMC
4-Jun-09 Thu		AM1(a) & AM3(a)			
5-Jun-09 Fri					
6-Jun-09 Sat					
7-Jun-09 Sun					
8-Jun-09 Mon					
9-Jun-09 Tue	AM1(a) & AM3(a)		TLLF(a)		
10-Jun-09 Wed		AM1(a) & AM3(a)			
11-Jun-09 Thu					
12-Jun-09 Fri					
13-Jun-09 Sat					
14-Jun-09 Sun					
15-Jun-09 Mon	AM1(a) & AM3(a)		TLLF(a)		
16-Jun-09 Tue		AM1(a) & AM3(a)			
17-Jun-09 Wed					
18-Jun-09 Thu				Monthly	
19-Jun-09 Fri					
20-Jun-09 Sat	AM1(a) & AM3(a)				
21-Jun-09 Sun					
22-Jun-09 Mon		AM1(a) & AM3(a)			
23-Jun-09 Tue					
24-Jun-09 Wed					
25-Jun-09 Thu					
26-Jun-09 Fri	AM1(a) & AM3(a)		TLLF(a)		
27-Jun-09 Sat		AM1(a) & AM3(a)			
28-Jun-09 Sun					
29-Jun-09 Mon					
30-Jun-09 Tue					

	Public Holiday
	Monitoring Day

**Contract No. HY/2007/14 Widening of Tuen Mun Road at Tsing Tin Interchange
Tentative Impact Monitoring Schedule (Jul 2009) Revision 1**

Date	Air Quality		Noise	Landscape & Visual	Weekly Site Inspection
	1-hour TSP	24-hours TSP	L _{Aeq} , 30 min		
1-Jul-09 Wed					
2-Jul-09 Thu	AM1(a) & AM3(a)		TLLF(a)		
3-Jul-09 Fri		AM1(a) & AM3(a)			
4-Jul-09 Sat					
5-Jul-09 Sun					
6-Jul-09 Mon					
7-Jul-09 Tue					
8-Jul-09 Wed	AM1(a) & AM3(a)		TLLF(a)		
9-Jul-09 Thu		AM1(a) & AM3(a)			
10-Jul-09 Fri					
11-Jul-09 Sat					
12-Jul-09 Sun					
13-Jul-09 Mon					
14-Jul-09 Tue	AM1(a) & AM3(a)		TLLF(a)		
15-Jul-09 Wed		AM1(a) & AM3(a)			
16-Jul-09 Thu					
17-Jul-09 Fri					
18-Jul-09 Sat					
19-Jul-09 Sun					
20-Jul-09 Mon	AM1(a) & AM3(a)		TLLF(a)		
21-Jul-09 Tue		AM1(a) & AM3(a)			
22-Jul-09 Wed					
23-Jul-09 Thu				Monthly	
24-Jul-09 Fri					
25-Jul-09 Sat	AM1(a) & AM3(a)				
26-Jul-09 Sun					
27-Jul-09 Mon		AM1(a) & AM3(a)			
28-Jul-09 Tue					
29-Jul-09 Wed					
30-Jul-09 Thu					
31-Jul-09 Fri	AM1(a) & AM3(a)		TLLF(a)		

	Public Holiday
	Monitoring Day
