


**ASB Biodiesel (Hong Kong) Limited**

**Development of a Biodiesel Plant at  
Tseung Kwan O Industrial Estate**

Monthly EM&A Report

October 2013

(Version 1.0)

Certified By   
(Environmental Team Leader)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties.

**CINOTECH CONSULTANTS LTD**

Room 1710, Technology Park,

18 On Lai Street,

Shatin, NT, Hong Kong

Tel: (852) 2151 2083 Fax: (852) 3107 1388

Email: [info@cinotech.com.hk](mailto:info@cinotech.com.hk)



**MANNINGS**  
(Asia) Consultants Limited

Address: 5/F, Winning Commercial Building, 46-48 Hillwood Road, Tsim Sha Tsui, Kowloon  
Tel: 852 - 3168 2028 Fax: 852 - 3168 2022

---

<i>To:</i>	Cinotech	<i>Date:</i>	28 November 2013
<i>Attn:</i>	Ms. Ivy Tam / Ms. Betty Choi	<i>Fax:</i>	3107 1388
<i>From:</i>	Mr. Mark Cheung	<i>Ref:</i>	D1067/H04497
<i>Job No.</i>	D1067	<i>Total Pages:</i>	1

---

**Subject: Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate  
Monthly EM&A Summary Report for October 2013**

---

Dear Madam,

We refer to your submission of the Monthly EM&A Report for October 2013 via email dated 15 November 2013.

We write to advise that we have no comment on the captioned report.

Regards,

Mark Cheung  
Independent Environmental Checker

KTC/gk

## TABLE OF CONTENTS

	<b>Page</b>
<b>EXECUTIVE SUMMARY .....</b>	<b>I</b>
Introduction .....	i
Environmental Monitoring and Audit Works .....	i
Environmental Licenses and Permits .....	i
Key Information in the Reporting Month.....	i
Future Key Issues .....	ii
<b>1 INTRODUCTION .....</b>	<b>1</b>
Background.....	1
Project Organizations .....	2
Construction Programme.....	3
Summary of EM&A Requirements .....	3
<b>2 ENVIRONMENTAL AUDIT .....</b>	<b>4</b>
Site Audits .....	4
Status of Environmental Licensing and Permitting.....	4
Status of Waste Management .....	4
Implementation Status of Environmental Mitigation Measures.....	4
Summary of Complaint and Prosecution.....	6
<b>3 CONCLUSIONS AND RECOMMENDATIONS .....</b>	<b>7</b>
Conclusions .....	7
Construction Program for the Next Months .....	7

### LIST OF TABLES

Table I	Summary Table for Key Information in the Reporting Month
Table 1.1	Key Project Contacts
Table 2.1	Summary of Environmental Licensing and Permit Status
Table 2.2	Observations and Recommendations of Site Audit

### LIST OF FIGURE

Figure 1.1	Site Layout Plan
------------	------------------

### LIST OF APPENDICES

Appendix A	Site Audit Summary
Appendix B	Updated Environmental Mitigation Implementation Schedule
Appendix C	Waste Generation in the Reporting Month
Appendix D	Complaint Log

## EXECUTIVE SUMMARY

### Introduction

1. This is the 53<sup>rd</sup> monthly Environmental Monitoring and Audit (EM&A) Report prepared by Cinotech Consultants Limited for Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate". This report documents the findings of EM&A Works conducted in October 2013.
2. The major site activities undertaken in the reporting month included:
  - General site cleaning and tidying.
  - OP Inspection
  - Fire Services Inspection

### Environmental Monitoring and Audit Works

3. Environmental monitoring and audit works for the Project were performed regularly as stipulated in the EM&A Manual and the results were checked and reviewed. The implementation of the environmental mitigation measures and environmental complaint handling procedures were also checked.

### Environmental Licenses and Permits

4. Licenses/Permits granted to the Project include the Environmental Permit (EP) for the Project. Environmental Permits No. EP-319/2009 and EP-319/2009/A were issued on 11 March 2009 and 7 April 2009 respectively. The Contractor has applied for the Registration of Chemical Waste Producer (WPN-5113-839-C1186-15), Construction Noise Permit (GW-RE0709-13), Wastewater Discharge License (WT00004508-2009), Notification of Works under APCO (337009) and Waste Discharge Account (7013917).

### Key Information in the Reporting Month

5. Summary of key information in this reporting month is tabulated in **Table I**.

**Table I Summary Table for Key Information in the Reporting Month**

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Complaint received	0	---	N/A	N/A	---
Changes to the assumptions and key construction / operation activities recorded	0	---	N/A	N/A	---
Status of submissions under EP	1	Monthly EM&A Report for September 2013	Submitted to EPD on 16 October 2013	Verified by IEC	---
Notifications of any summons & prosecutions	0	---	N/A	N/A	---

**Future Key Issues**

6. Construction work has been substantially completed. No major site activities will be carried out in the coming months.

## 1 INTRODUCTION

### Background

- 1.1 Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate is a Designated Project (hereafter referred to as “the Project”) under the Environmental Impact Assessment Ordinance (Cap. 449). A study of environmental impact assessment (EIA) was undertaken to consider the key issues of air quality, noise, water quality, ecological and identify possible mitigation measures associated with the works. An EIA Report was approved by the Environmental Protection Department (EPD) on 26 February 2009.
- 1.2 The project is to construct and operate a 100,000 tonnes per annum biodiesel plant at Tseung Kwan O Industrial Estate. The plant will use a multi-feedstock which consists of waste cooking oil (WCO), oil and grease recovered from grease trap waste (GTW), Palm Fatty Acid Distillate (PFAD) and animal fats. The proposed biodiesel plant not only offers a convenient recycling outlet for GTW and WCO but also converts the oil and grease recovered from these wastes into useful products. The Project also offers a cleaner alternative to diesel fuel to the Hong Kong market. The main processes include the followings:-
- Construction of feedstock reception and storage facilities, and offices;
  - Construction of a grease trap waste pre-treatment facility (with a designated treatment capacity of about 200,000 tonnes per annum);
  - Construction of a wastewater treatment plant (with a designed treatment capacity of about 170,000 m<sup>3</sup> per annum);
  - Installation of biodiesel production and glycerine purification system;
  - Construction of product storage and ancillary facilities;
  - Pretreatment of grease trap waste;
  - Treatment of wastewater generated from feedstock pre-treatment and glycerine dewatering process, and filtrates from dewatering process of sludge treatment;
  - Transesterification of feedstock with alcohol-catalyst; and
  - Purification of biodiesel.
- 1.3 The general layout of the Project is shown in **Figure 1.1**.
- 1.4 Layout plan of tank farm **2A, 2B to 2E** is revised and a report is made by Environmental Resources Management (ERM) regarding such change. The report concluded that no deviation is found from the approved EIA report.
- 1.5 Environmental Permits (EP) No. EP-319/2009, EP-319/2009/A and EP-319/2009/B were issued on 11 March 2009, 7 April 2009 and 31 Jan 2013 respectively for Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate to ASB Biodiesel (Hong Kong) Limited as the Permit Holder. A VEP was submitted and the latest EP No. EP-319/2009/C was issued by EPD on 5 Mar 2013.
- 1.6 Cinotech Consultants Limited was commissioned by the Contractor to undertake the Environmental Monitoring and Audit (EM&A) works for the Project. This is the 53<sup>rd</sup> Monthly EM&A report summarizing the EM&A works for the Project in October 2013.

## Project Organizations

1.7 Different parties with different levels of involvement in the project organization include:

- Project Proponent – ASB Biodiesel (Hong Kong) Limited
- Project Manager – AECOM
- Contractor – China Harbour Engineering Company Limited (CHEC)
- Environmental Team (ET) – Cinotech Consultants Limited
- Independent Environmental Checker (IEC) – Mannings (Asia) Consultants Ltd.

1.8 The responsibilities of respective parties are detailed in Section 1.10 of the Final EM&A Manual of the Project.

1.9 The key contacts of the Project are shown in **Table 1.1**.

**Table 1.1 Key Project Contacts**

Party	Role	Name	Position	Phone No.	Fax No.
ASB	Project Proponent	Ms. Sylvia Har	Senior Plant Engineer	9479 0949	3741 1661
Cinotech	Environmental Team	Dr. HF Chan	ET Leader	2151 2088	3107 1388
		Ms. Ivy Tam	Project Coordinator	2151 2090	
		Ms. Betty Choi	Audit Team Leader	2151 2072	
Mannings	Independent Environmental Checker	Mr. Mark Cheung	Independent Environmental Checker	3168 2028	3168 2022
		Mr. Gavin Kwok	Assistant to Independent Environmental Checker	3168 2028	
AECOM	Project Manager	Mr. Matthew Lau	Construction Manager	9363 5586	N/A
CHEC	Contractor	Mr. Peter Chung	Project Manager	9471 2438	2623 9226
		Mr. Anson Wong	Safety and Environmental Officer	9656 3837	
		Mr. Simon Li	Environmental Supervisor (Ass. Planning Engineer)	6152 7867	

### **Construction Programme**

1.10 The site activities undertaken in the reporting month were:

- General site cleaning and tidying.
- OP Inspection
- Fire Services Inspection

### **Summary of EM&A Requirements**

1.11 The EM&A requirements are described in the following sections, including:

- Environmental mitigation measures, as recommended in the project EIA study final report; and
- Environmental requirements in contract documents.

1.12 The advice on the implementation status of environmental protection and pollution control/ mitigation measures is summarized in Section 3 of this report.



## 2 ENVIRONMENTAL AUDIT

### Site Audits

- 2.1 Site audits were carried out by ET on monthly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summary of the site audit in this reporting month is attached in **Appendix A**.
- 2.2 Site audit was conducted on 31<sup>st</sup> October 2013 by ET in the reporting month. No non-compliance was observed during the site audits.

### Status of Environmental Licensing and Permitting

- 2.3 All permits/licenses obtained for the Project are summarized in **Table 2.1**.

### Status of Waste Management

- 2.4 Armour rock in this project was reused in a CEDD project CV/2010/03. The transportation record of armour rock and the quantities of all waste generated in this reporting month are summarized in **Appendix C**.

### Implementation Status of Environmental Mitigation Measures

- 2.5 According to the EIA Study Report, Environmental Permit and the EM&A Manual of the Project, the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An updated summary of the EMIS is provided in **Appendix B**.

**Table 2.1 Summary of Environmental Licensing and Permit Status**

Permit / License No.	Valid Period		Details	Status
	From	To		
<b>Environmental Permit (EP)</b>				
EP-319/2009/A	07/04/2009	N/A	Construction and operation of (i) a biochemical plant with a storage capacity of more than 500 tonnes and in which substances are processed and produced; (ii) a storage, transfer and trans-shipment of oil facility with a storage capacity of not less than 1,000 tonnes; and (iii) a dangerous goods godown with a storage capacity exceeding 500 tonnes .	Valid
<b>Registration of Chemical Waste Producer</b>				
WPN-5113-839-C1186-15	12/06/2009	-	Spent Lubrication oil.	Valid
<b>Construction Noise Permit (CNP)</b>				
GW-RE0709-13	02/07/2013	19/01/2014	Use of Powered Mechanical Equipment during 0000-2400 hours on general holidays (including Sundays), 0000-0700 hours and 1900-2400 hours on any day not being a general holiday.	Valid
<b>Wastewater Discharge License</b>				
WT00004508-2009	07/09/2009	-	Discharge of wastewater from construction site including wheel washing water and chemical precipitation tank	Valid
<b>Billing Account for Disposal of Construction Waste</b>				
A/C No.: 7013917	-	-	-	Valid
<b>Notification of Works under APCO</b>				
Ref. no.: 337009	26/10/2011	-	-	Valid

- 2.6 During the site inspection in the reporting month, no non-conformance was identified. The observations and recommendations made during the audit session are summarized in **Table 2.2**.

**Table 2.2 Observations and Recommendations of Site Audit**

<b>Parameters</b>	<b>Date</b>	<b>Observations and Recommendations</b>	<b>Follow-up</b>
N/A	N/A	N/A	N/A

### **Summary of Complaint and Prosecution**

- 2.7 No environmental related complaint, prosecution or notification of summons was received in the reporting month.
- 2.8 Since the Project commencement, there were a total of 5 project-related environmental complaints. No prosecution or notification of summons was received since the Project commencement. The Complaint Log is attached in **Appendix D**.

### **3 CONCLUSIONS AND RECOMMENDATIONS**

#### **Conclusions**

- 3.1 Environmental audit works were conducted in the reporting month. Site inspections were conducted on monthly basis. The results were reviewed and checked.
- 3.2 No environmental complaint, prosecution or notification of summons was received.

#### **Construction Program for the Next Months**

- 3.3 Construction work has been substantially completed. No major site activities will be carried out in the coming months. No key environmental issue is anticipated.

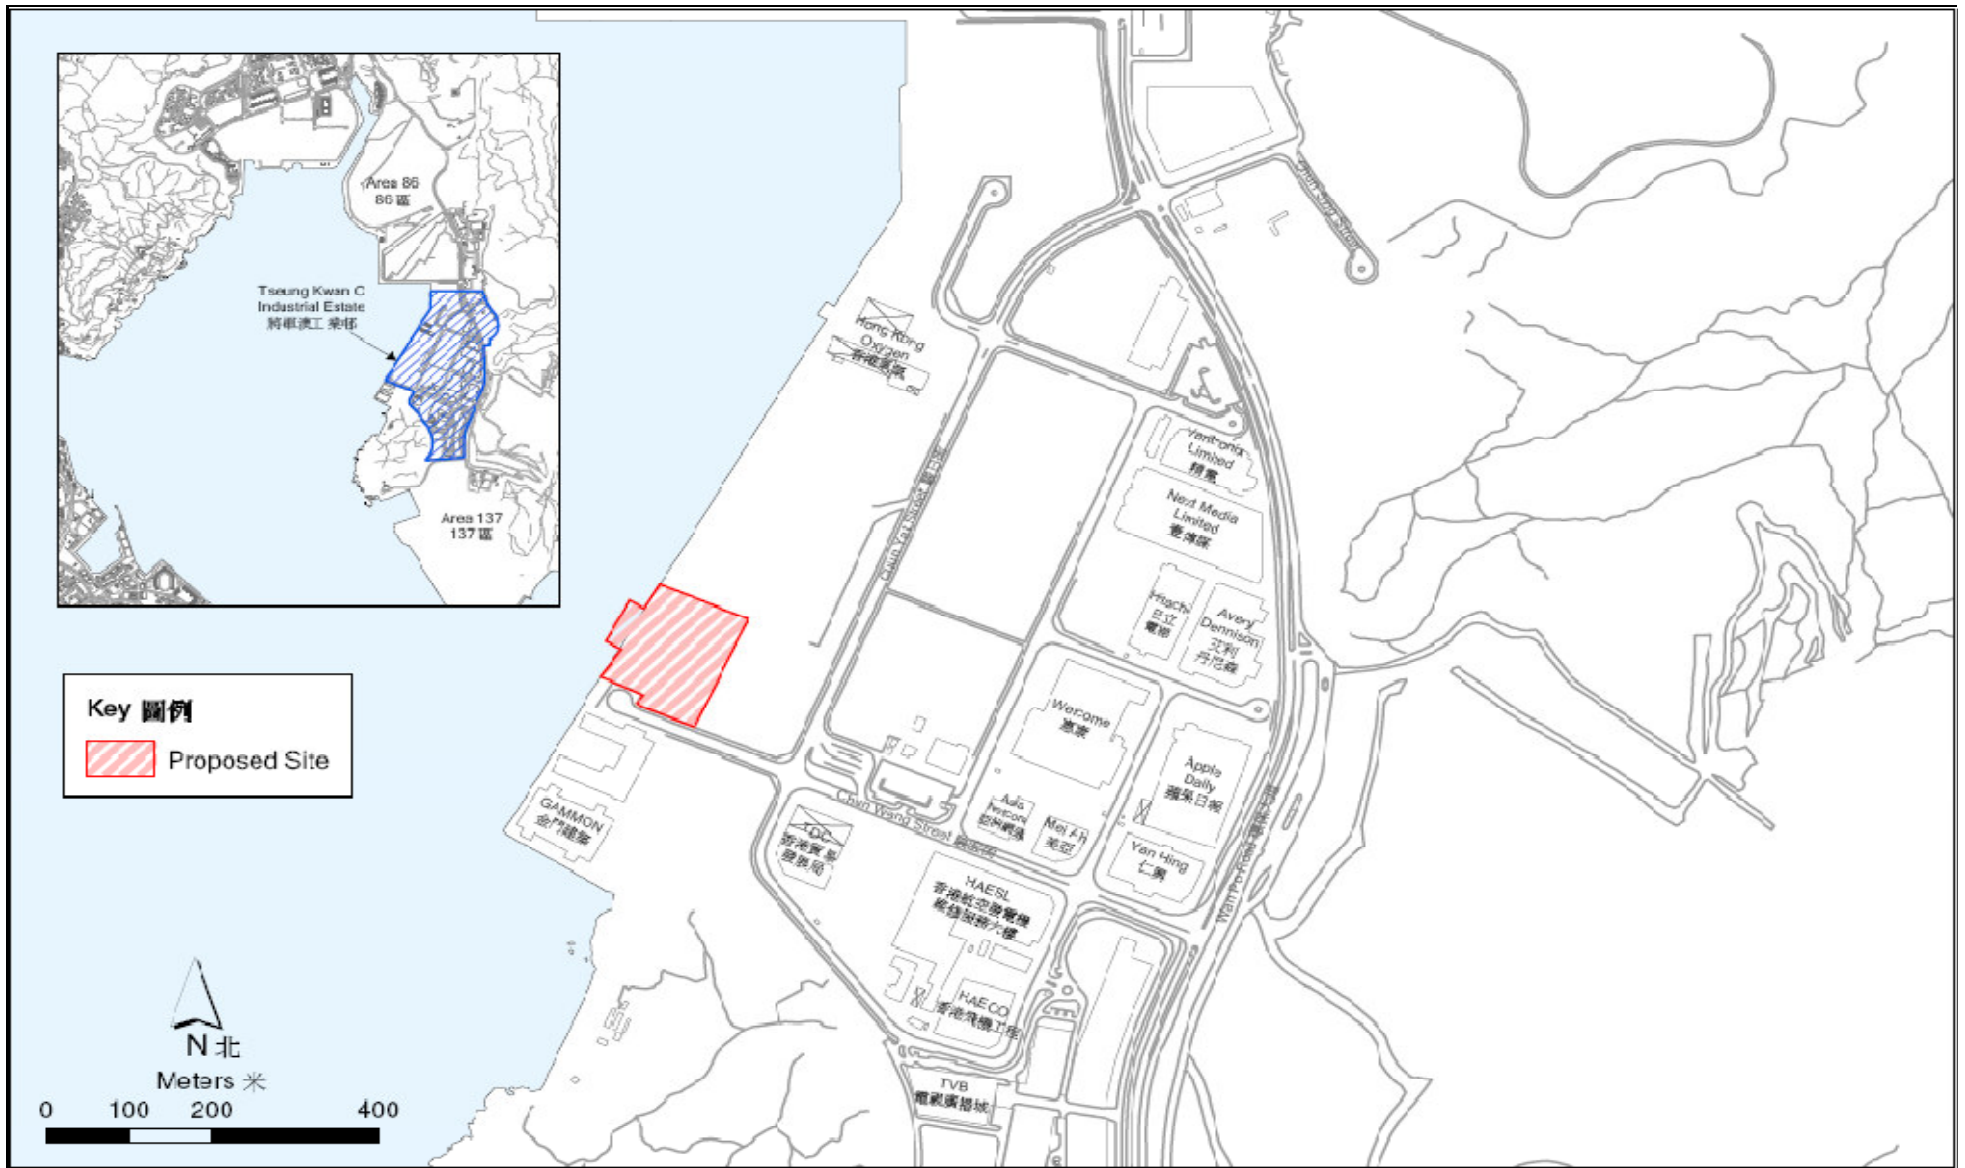
---

---

## FIGURES

---

---



**Key 圖例**  
 Proposed Site

Title	Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate		Scale	N.T.S	Project No.	MA9021	<b>CINOTECH</b>
	Site Layout Plan		Date	Jun-09	Figure	1.1	

---

---

**APPENDIX A  
SITE AUDIT SUMMARY**

---

---

## Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate



### Monthly Site Inspection Record Summary

#### Inspection Information

Checklist Reference Number	131031
Date	31 October 2013 (Thursday)
Time	16:20 – 16:40

Ref. No.	Non-Compliance	Related Item No.
-	None	-

Ref. No.	Remarks/Observations	Related Item No.
	<p><b>A. Water Quality</b></p> <ul style="list-style-type: none"> <li>• No environmental deficiency was identified during site inspection.</li> </ul> <p><b>B. Air Quality</b></p> <ul style="list-style-type: none"> <li>• No environmental deficiency was identified during site inspection.</li> </ul> <p><b>C. Noise</b></p> <ul style="list-style-type: none"> <li>• No environmental deficiency was identified during site inspection.</li> </ul> <p><b>D. Waste / Chemical Management</b></p> <ul style="list-style-type: none"> <li>• No environmental deficiency was identified during site inspection.</li> </ul> <p><b>E. Permit / Licenses</b></p> <ul style="list-style-type: none"> <li>• No environmental deficiency was identified during site inspection.</li> </ul> <p><b>F. Reminders</b></p> <ul style="list-style-type: none"> <li>• No environmental deficiency was identified during site inspection.</li> </ul> <p><b>G. Others</b></p> <ul style="list-style-type: none"> <li>Follow-up on previous audit section (Ref. No.:130927):</li> <li>• No environmental deficiency was observed during the previous site audit.</li> </ul>	

	Name	Signature	Date
Recorded by	Betty Choi		1 November 2013
Checked by	Dr. HF Chan		1 November 2013



---

---

**APPENDIX B  
UPDATED ENVIRONMENTAL  
MITIGATION IMPLEMENTATION  
SCHEDULE**

---

---

**Appendix B - Summary of Environmental Mitigation Implementation Schedule (Construction Phase)**

Types of Impacts	Mitigation Measures	Status
<b>Construction Dust</b>	<ul style="list-style-type: none"> <li>• Dust control measures such as water spaying on roads and dusty areas, covering of lorries by impervious sheets and controlling of the falling height of fill materials will be implemented;</li> <li>• Effective dust screens, sheeting or netting will be provided to enclose the scaffolding from the ground level of the facility during the building construction;</li> <li>• All debris and materials will be covered or stored in a sheltered debris collection area;</li> <li>• Hoarding from ground level will be provided along the entire length of the site boundary except for a site entrance or exit;</li> <li>• Every stockpile of dusty materials will be covered entirely by impermeable sheeting or placed in an area sheltered on the top and the 3 sides;</li> <li>• Regular maintenance and checking of the diesel powered mechanical equipment will be adopted to avoid any black smoke emissions and to minimize gaseous emissions.</li> <li>• Monthly site audits will be conducted to ensure the implementation of suitable dust control measures and good site practices.</li> </ul>	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p>
<b>Construction Noise</b>	<ul style="list-style-type: none"> <li>• Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction program;</li> <li>• Silencers or mufflers on construction equipment will be utilized and will be properly maintained during the construction program;</li> <li>• Mobile plant, if any, will be sited as far from NSRs as possible;</li> <li>• Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum;</li> <li>• Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>• Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from onsite construction activities.</li> </ul>	<p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p> <p>^</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
 N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
 \* Recommendation was made during site audit but improved/rectified by the contractor;  
 # Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
Water Quality	<p><u>Piling Activities</u></p> <ul style="list-style-type: none"> <li>Silt curtain will be installed around the marine piling area to contain any suspended mud and sediments generated during the piling works. Silt removal facilities such as silt traps or sedimentation facilities will be provided to remove silt particles from groundwater (if pumping is required) to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities will be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms.</li> </ul>	^
	<p><u>Construction Site Run-off and Drainage</u></p> <ul style="list-style-type: none"> <li>Silt removal facilities such as silt traps or sedimentation facilities will be provided to remove silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities will be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms.</li> <li>Careful programming of the works to minimise surface excavations for the construction works during the wet season. If excavation of soil cannot be avoided during the wet season, exposed slope surfaces will be covered by a tarpaulin or other means. Other measures that need to be implemented before, during, and after rainstorms are summarised in ProPECC PN 1/94.</li> <li>Exposed soil surfaces will be protected by paving or fill material as soon as possible to reduce the potential of soil erosion.</li> <li>Open stockpiles of construction materials or construction wastes on-site of more than 50m<sup>3</sup> will be covered with tarpaulin or similar fabric during rainstorms. These materials will not be placed near the seawall area.</li> </ul>	^ ^ ^ ^
	<p><u>General Construction Activities</u></p> <ul style="list-style-type: none"> <li>Debris and refuse generated on-site will be collected, handled and disposed of properly to avoid entering the nearby water sensitive receivers (WSRs). Stockpiles of cement and other construction materials will be kept covered when not being used.</li> <li>Oils and fuels will only be used and stored in designated areas which have pollution prevention facilities. All fuel tanks and storage areas will be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund will be drained of rainwater after a rain event.</li> </ul>	^ ^

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

Types of Impacts	Mitigation Measures	Status
	<p data-bbox="394 225 902 252"><u>Sewage generated from On-site Workforce</u></p> <ul data-bbox="443 296 1980 427" style="list-style-type: none"> <li data-bbox="443 296 1980 360">• Temporary sanitary facilities, such as portable chemical toilets, will be provided on-site. A specialised contractor will be responsible for regular collection and appropriate disposal of the sewage and maintenance of these facilities.</li> <li data-bbox="443 363 1980 427">• Monthly site inspections will be carried out during construction to ensure that the mitigation measures listed above are properly implemented. The site audit frequency will be increased to weekly intervals during the piling works.</li> </ul>	<p data-bbox="2056 296 2078 316">^</p> <p data-bbox="2056 363 2078 383">^</p>
<p data-bbox="215 488 315 515"><b>Ecology</b></p>	<ul data-bbox="443 472 1980 563" style="list-style-type: none"> <li data-bbox="443 472 1980 563">• Mitigation measures for minimising water quality impacts are presented in detail above. These measures will be properly implemented and good construction practices will be adopted to minimise potential adverse impacts to marine ecological resources.</li> </ul>	<p data-bbox="2056 488 2078 507">^</p>

Remarks: ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;  
N/A Not Applicable at this stage; • Non-compliance but rectified by the contractor;  
\* Recommendation was made during site audit but improved/rectified by the contractor;  
# Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

---

---

**APPENDIX C  
WASTE GENERATION IN THE  
REPORTING MONTH**

---

---

**Monthly Summary Waste Flow Table**  
**For Contract 270 Biodiesel Plant Tseung Kwan O Project**  
**Reporting Year: 2013**

Month	Actual Quantities of Inert C&D Materials Generated / Imported (in '000 m <sup>3</sup> )						Actual Quantities of Other C&D Materials / Wastes Generated				
	Total Quantities Generated [a+b+c+d]	Broken Concrete (including rock for recycling into aggregates) ( a )	Reused in the Contract ( b )	Reused in Other Projects ( c )	Disposed as Public Fill ( d )	Imported C&D Material	Metal (in '000 kg)	Paper/ cardboard packaging (in '000kg)	Plastics (bottles/containers, plastic sheets/ foams from package material) (in '000kg)	Chemical Waste (in '000kg)	Others (e.g. General Refuse etc.) (in '000m3)
January	0	0	0	0	0	0	0	0.005	0	0	0.082
February	0	0	0	0	0	0	0	0.004	0	0	0.020
March	0	0	0	0	0	0	0	0.004	0	0	0.053
April	0	0	0	0	0.918	0	0	0.003	0	0	0.023
May	0	0	0	0	1.962	0	0	0.004	0	0	0.078
June	0	0	0	0	0.966	0	0	0.003	0	0	0.089
<b>Half-year Total</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>3.846</b>	<b>0</b>	<b>0</b>	<b>0.023</b>	<b>0</b>	<b>0</b>	<b>0.345</b>
July	0	0	0	0	0.035	0	0	0.013	0	0	0.101
August	0	0	0	0	0.157	0	0	0.021	0	0	0.768
September	0	0	0	0	0.006	0	0	0.005	0	0	0.066
October	0	0	0	82.65 tons*	0.003	0	0	0.002	0	0	0.084
November											
December											
<b>Yearly Total</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>82.65 tons</b>	<b>4.047</b>	<b>0</b>	<b>0</b>	<b>0.064</b>	<b>0</b>	<b>0</b>	<b>1.364</b>

\* Reuse of armour rock in CEDD project CV/2010/03

---

---

**APPENDIX D  
COMPLAINT LOG**

---

---

**APPENDIX D – COMPLAINT LOG**

Reporting Month: October 2013

Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
COM-2012-08-001	Jetty Area	28-08-2012	A resident in Lohas Park complained about noise nuisance from the site.	Investigation by EPD identified the source to be chiselling work at the jetty area. Although the chisel machines were covered by valid CNP, the Contractor decided to suspend the corresponding work during restricted hours. The machine was later covered by sound proof canvas to minimize noise transmission. Subsequent inspection and noise measurement by the EPD on 3 <sup>rd</sup> September 2012 concluded that the noise reduction measure was effective and acceptable at Lohas Park.	Closed
COM-2012-09-002	Jetty Area	07-09-2012	A resident in Lohas Park complained about noise nuisance from the site.	Investigation by EPD identified the source to be chiselling work at the jetty area. Only one chisel machine was operated on the day of complain and it was screened by sound proof canvas. Although the machine was covered by valid CNP, the Contractor decided to suspend the corresponding work during restricted hours during investigation period. Subsequent inspection and noise measurement (daytime at site, night time at Lohas Park) by the EPD on 12 <sup>th</sup> September 2012 concluded that the noise levels were acceptable at Lohas Park.	Closed
COM-2012-09-003	Jetty Area	27-09-2012	A resident in Lohas Park complained about noise nuisance from the site.	The chisel machine used at JP3 of the jetty area was identified as the noise source. According to the Contractor, the machine was screened by sound proof canvas. Although the machine was covered by valid CNP, the Contractor decided to carry out the corresponding work during normal operation hours only. This was agreed with the complainant in Lohas Park.	Closed
COM-2012-09-004	Not Specified	04-10-2012	A resident in Lohas Park complained about noise nuisance from the site at	According to the Contractor, According to the Contractor, only one drilling machine and chiselling machine were in use, which were covered by valid CNP. We advised the Contractor to communicate with the residents in Lohas	Closed



Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
			11:18pm.	Park given consistent noise complains. The Contractor explained to the complainant that chiselling work will stop at 11pm every day and start after 10am during weekends to minimize noise nuisance. Further in November, a noise enclosure was erected to cover the noisy part of the chiselling machine.	
Com-2012-11-005	Jetty Area	23-11-2012	A resident in Lohas Park complained about noise nuisance from the site at around 3:00 am	The chisel machine used of the jetty area was identified as the noise source. According to the Contractor, the machine was screened by enclosure. Although the machine was covered by valid CNP, the Contractor decided to carry out the corresponding work during 7:00 – 23:00. Contractor explained to the complainant that the bored piling will be completed in early December.	Closed

Remarks: N/A
