



China Harbour Engineering Company Limited

Contract No. HY/2010/02

**Hong Kong – Zhuhai – Macao Bridge
Hong Kong Boundary Crossing
Facilities –
Reclamation Works****Monthly EM&A Report for May 2014**

[06/2014]

	Name	Signature
Prepared & Checked:	Y T Tang	
Reviewed, Approved and Certified:	Echo Leong (ETL)	

Version:	Rev. 0	Date:	16 June 2014
Disclaimer <p>This report is prepared for China Harbour Engineering Company Limited and is given for its sole benefit in relation to and pursuant to Contract No. HY/2010/02 Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities-Reclamation Works and may not be disclosed to, quoted to or relied upon by any person other than China Harbour Engineering Company Limited without our prior written consent. No person (other than China Harbour Engineering Company Limited) into whose possession a copy of this report comes may rely on this report without our express written consent and China Harbour Engineering Company Limited may not rely on it for any purpose other than as described above.</p>			

AECOM Asia Co. Ltd. 15/F, Grand Central Plaza, Tower 1, 138 Shatin Rural Committee Road, Shatin, NT, Hong Kong Tel: (852) 3922 9000 Fax: (852) 2317 7609 www.aecom.com
--

Ref.: HYDHZMBEEM00_0_2008L.14

16 June 2014

Engineer's Representative
Ove Arup & Partners
Chief Resident Engineer's Office
5 Ying Hei Road, Tung Chung, Lantau
Hong Kong

By Fax (3698 5999) and By Post

Attention: Mr. Roger Marechal

Dear Mr. Marechal,

**Re: Agreement No. CE 48/2011 (EP)
Environmental Project Office for the
HZMB Hong Kong Link Road, HZMB Hong Kong Boundary Crossing Facilities,
and Tuen Mun-Chek Lap Kok Link – Investigation**

**Contract No. HY/2010/02
Hong Kong – Zhuhai – Macao Bridge
Hong Kong Boundary Crossing Facilities – Reclamation Work
Monthly Environmental Monitoring & Audit Report for May 2014**

Reference is made to the Environmental Team's submission of the Monthly Environmental Monitoring & Audit Report for May 2014 (letter ref. 60249820/C/RMKY14061601 dated 16 June 2014) copied to us by E-mail on 13 June 2014.

We are pleased to inform you that we have no adverse comment on the captioned Monthly EM&A Report. We write to verify the captioned report in accordance with Condition 5.4 of EP-353/2009/G and Condition 4.4 of EP-354/2009/B (for TM-CLKL Southern Landfall Reclamation only).

ET is reminded to ensure all information reported are true, valid and correct before sending to this office for review.

Thank you very much for your kind attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,



Raymond Dai
Independent Environmental Checker

c.c.	HyD	Mr. Matthew Fung	(By Fax: 3188 6614)
	HyD	Mr. Wai-ping Lee	(By Fax: 3188 6614)
	AECOM	Ms. Echo Leong	(By Fax: 2317 7609)
	CHEC	Mr. Lim Kim Chuan	(By Fax: 2578 0413)

T:\Projects\HYDHZMBEEM00\02_Proj_Mgt\02_Corr\HYDHZMBEEM00_0_2008L.14.docx

TABLE OF CONTENTS

	Page
EXECUTIVE SUMMARY	1
1 INTRODUCTION	4
1.1 Background	4
1.2 Scope of Report	4
1.3 Project Organization	5
1.4 Summary of Construction Works	5
1.5 Summary of EM&A Programme Requirements	6
2 AIR QUALITY MONITORING	7
2.1 Monitoring Requirements	7
2.2 Monitoring Equipment	7
2.3 Monitoring Locations	7
2.4 Monitoring Parameters, Frequency and Duration	8
2.5 Monitoring Methodology	8
2.6 Monitoring Schedule for the Reporting Month	10
2.7 Results and Observations	10
3 NOISE MONITORING	11
3.1 Monitoring Requirements	11
3.2 Monitoring Equipment	11
3.3 Monitoring Locations	11
3.4 Monitoring Parameters, Frequency and Duration	12
3.5 Monitoring Methodology	12
3.6 Monitoring Schedule for the Reporting Month	12
3.7 Monitoring Results	13
4 WATER QUALITY MONITORING	14
4.1 Monitoring Requirements	14
4.2 Monitoring Equipment	14
4.3 Monitoring Parameters, Frequency and Duration	14
4.4 Monitoring Locations	15
4.5 Monitoring Methodology	16
4.6 Monitoring Schedule for the Reporting Month	17
4.7 Results and Observations	17
5 DOLPHIN MONITORING	19
5.1 Monitoring Requirements	19
5.2 Monitoring Equipment	19
5.3 Monitoring Frequency and Conditions	19
5.4 Monitoring Methodology and Location	19
5.5 Monitoring Procedures	21
5.6 Monitoring Schedule for the Reporting Month	21
5.7 Results and Observations	21
6 ENVIRONMENTAL SITE INSPECTION AND AUDIT	25
6.1 Site Inspection	25
6.2 Advice on the Solid and Liquid Waste Management Status	27
6.3 Environmental Licenses and Permits	28
6.4 Implementation Status of Environmental Mitigation Measures	28
6.5 Summary of Exceedances of the Environmental Quality Performance Limit	29
6.6 Summary of Complaints, Notification of Summons and Successful Prosecutions	29
7 FUTURE KEY ISSUES	31
7.1 Construction Programme for the Coming Months	31
7.2 Key Issues for the Coming Month	32
7.3 Monitoring Schedule for the Coming Month	32

8	CONCLUSIONS AND RECOMMENDATIONS	33
8.1	Conclusions	33
8.2	Recommendations	34

List of Tables

Table 1.1	Contact Information of Key Personnel
Table 2.1	Air Quality Monitoring Equipment
Table 2.2	Locations of Impact Air Quality Monitoring Stations
Table 2.3	Air Quality Monitoring Parameters, Frequency and Duration
Table 2.4	Summary of 1-hour TSP Monitoring Results in the Reporting Period
Table 2.5	Summary of 24-hour TSP Monitoring Results in the Reporting Period
Table 3.1	Noise Monitoring Equipment
Table 3.2	Locations of Impact Noise Monitoring Stations
Table 3.3	Noise Monitoring Parameters, Frequency and Duration
Table 3.4	Summary of Construction Noise Monitoring Results in the Reporting Period
Table 4.1	Water Quality Monitoring Equipment
Table 4.2	Impact Water Quality Monitoring Parameters and Frequency
Table 4.3	Impact Water Quality Monitoring Stations
Table 4.4	Laboratory Analysis for Suspended Solids
Table 4.5	Summary of Water Quality Exceedances
Table 5.1	Dolphin Monitoring Equipment
Table 5.2	Impact Dolphin Monitoring Line Transect Co-ordinates (Provided by AFCD)
Table 5.3	Impact Dolphin Monitoring Survey Effort Summary, Effort by Area and Beaufort Sea State
Table 5.4	Impact Dolphin Monitoring Survey Details May 2014
Table 5.5	The Encounter Rate of Number of Dolphin Sightings & Total Number of Dolphins per Area^
Table 6.1	Summary of Environmental Licensing and Permit Status

Figures

Figure 1	General Project Layout Plan
Figure 2	Impact Air Quality and Noise Monitoring Stations and Wind Station
Figure 3	Impact Water Quality Monitoring Stations
Figure 4	Impact Dolphin Monitoring Line Transect Layout Map
Figure 5	Impact Dolphin Monitoring Survey Efforts and Sightings in May 2014
Figure 6	Environmental Complaint Handling Procedures

List of Appendices

Appendix A	Project Organization for Environmental Works
Appendix B	Three Month Rolling Construction Programmes
Appendix C	Implementation Schedule of Environmental Mitigation Measures (EMIS)
Appendix D	Summary of Action and Limit Levels
Appendix E	Calibration Certificates of Monitoring Equipments
Appendix F	EM&A Monitoring Schedules
Appendix G	Impact Air Quality Monitoring Results and their Graphical Presentation
Appendix H	Meteorological Data for Monitoring Periods on Monitoring Dates in May 2014
Appendix I	Impact Construction Noise Monitoring Results and their Graphical Presentation
Appendix J	Impact Water Quality Monitoring Results and their Graphical Presentation
Appendix K	Impact Dolphin Monitoring Survey Sighting Summary
Appendix L	Event Action Plan
Appendix M	Monthly Summary of Waste Flow Table
Appendix N	Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions

EXECUTIVE SUMMARY

Contract No. HY/2010/02 – Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities – Reclamation Work (here below, known as “the Project”) mainly comprises reclamation at the northeast of the Hong Kong International Airport of an area of about 130-hectare for the construction of an artificial island for the development of the Hong Kong Boundary Crossing Facilities (HKBCF), and about 19-hectare for the southern landfall of the Tuen Mun - Chek Lap Kok Link (TMCLKL). It is a designated project and is governed by the current permits for the Project, i.e. the amended Environmental Permits (EPs) issued on 06 August 2013 (EP-353/2009/G) and 28 January 2014 (EP-354/2009/B) (for TMCLKL Southern Landfall Reclamation only).

Ove Arup & Partners Hong Kong Limited (Arup) was appointed by Highways Department (HyD) as the consultants for the design and construction assignment for the Project’s reclamation works (i.e. the Engineer for the Project).

China Harbour Engineering Company Limited (CHEC) was awarded by HyD as the Contractor to undertake the construction work of the Project.

ENVIRON Hong Kong Ltd. was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO) for the Project.

AECOM Asia Co. Ltd. (AECOM) was appointed by CHEC to undertake the role of Environmental Team for the Project for carrying out the environmental monitoring and audit (EM&A) works.

The construction phase of the Project under the EPs was commenced on 12 March 2012 and will be tentatively completed by early Year 2016. The EM&A programme, including air quality, noise, water quality and dolphin monitoring and environmental site inspections, was commenced on 12 March 2012.

This report documents the findings of EM&A works conducted in the period between 1 and 31 May 2014. As informed by the Contractor, major activities in the reporting period were:-

Marine-based Works

- Cellular structure installation
- Connecting arc cell installation
- Laying geo-textile
- Sand blanket laying
- Sand filling
- Maintenance of silt curtain & silt screen at sea water intake of HKIA
- Stone column installation
- Band drain installation
- Backfill cellular structure
- Geotechnical Instrumentation works
- Surcharge laying
- Vibro-compaction on surcharge
- Capping Beams structures
- Construction of Conveyors for public fill
- Portion D Construction of Access to Portion A

Land-based Works

- Maintenance works of Site Office at Works Area WA2
- Maintenance works of Public Works Regional Laboratory at Works Area WA3
- Geo-textile fabrication at Works Area WA2
- Installed sand bag at Works Area WA2
- Maintenance of Temporary Marine Access at Works Area WA2

A summary of monitoring and audit activities conducted in the reporting period is listed below:

24-hour Total Suspended Particulates (TSP) monitoring	6 sessions
1-hour TSP monitoring	6 sessions
Noise monitoring	4 sessions
Impact water quality monitoring	13 sessions

Impact dolphin monitoring	2 surveys
Joint Environmental site inspection	5 sessions

Breaches of Action and Limit Levels for Air Quality

All 1-Hour TSP and 24-hour TSP results were below the Action and Limit Level in the reporting month.

Breaches of Action and Limit Levels for Noise

For construction noise, no exceedance was recorded at all monitoring stations in the reporting period.

Breaches of Action and Limit Levels for Water Quality

For impact water quality monitoring, no exceedance was recorded at all monitoring stations in the reporting period.

Impact Dolphin Monitoring

A total of three sightings were made, two “opportunistic” and one “on effort”. All sightings were made on the 31 May 14. A total of eighteen individuals were sighted from the two impact dolphin surveys in the reporting period. Sighting details are summarised and plotted in Appendix K and Figure 5c, respectively.

Behaviour: Of the three sightings, two groups were feeding and the third engaged in multiple activities which included milling and feeding. The locations of sighting with different behaviour are mapped in Figure 5d.

One (1) Limit Level Exceedance of dolphin monitoring was noted. The investigation is undergoing and the investigation results will be reported in the quarterly EM&A report (Mar 14 – May 14).

Complaint, Notification of Summons and Successful Prosecution

As informed by the Contractor on 7 May 14, a complaint was received by the Contractor on 17 April 14 concerning sand and dust emission from uncovered barges parking at the sea area off the Tuen Mun Ferry Pier. Investigation result shows that the complaint is unlikely to be related to this Contract.

As informed by the Contractor on 30 May 14, an environmental complaint had been received on 28 May 2014. The complainant mentioned that waste such as earth and concrete were being felled into the sea everyday at the Hong Kong-Zhuhai-Macao Bridge at location where construction works are being conducted, causing pollution to the marine environment. After investigation, it is concluded that the complaint is unlikely to be related to this Contract.

No notification of summons or prosecution was received in the reporting period.

Reporting Change

There was no reporting change required in the reporting period.

Future Key Issues

Key issues to be considered in the coming month included:-

- Site runoff should be properly collected and treated prior to discharge;
- Minimize loss of sediment from filling works;
- Regular review and maintenance of silt curtain systems, drainage systems and desilting facilities;
- Exposed surfaces/soil stockpiles should be properly treated to avoid generation of silty surface run-off during rainstorm;
- Regular review and maintenance of wheel washing facilities provided at all site entrances/exits;
- Conduct regular inspection of various working machineries and vessels within works areas to avoid any dark smoke emission;
- Suppress dust generated from work processes with use of bagged cements, earth movements, excavation activities, exposed surfaces/soil stockpiles and haul road traffic;
- Quieter powered mechanical equipment should be used;
- Provision of proper and effective noise control measures for operating equipment and machinery on-site,

such as erection of movable noise barriers or enclosure for noisy plants;

- Closely check and replace the sound insulation materials regularly;
- Better scheduling of construction works to minimize noise nuisance;
- Properly store and label oil drums and chemical containers placed on site;
- Proper chemicals, chemical wastes and wastes management;
- Maintenance works should be carried out within roofed, paved and confined areas;
- Collection and segregation of construction waste and general refuse on land and in the sea should be carried out properly and regularly; and
- Proper protection and regular inspection of existing trees, transplanted/retained trees.

1 INTRODUCTION

1.1 Background

- 1.1.1 Contract No. HY/2010/02 – Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities – Reclamation Work (here below, known as “the Project”) mainly comprises reclamation at the northeast of the Hong Kong International Airport of an area of about 130-hectare for the construction of an artificial island for the development of the Hong Kong Boundary Crossing Facilities (HKBCF), and about 19-hectare for the southern landfall of the Tuen Mun - Chek Lap Kok Link (TMCLKL).
- 1.1.2 The environmental impact assessment (EIA) reports (Hong Kong – Zhuhai – Macao Bridge Hong Kong Boundary Crossing Facilities – EIA Report (Register No. AEIAR-145/2009) (HKBCFEIA) and Tuen Mun – Chek Lap Kok Link – EIA Report (Register No. AEIAR-146/2009) (TMCLKLEIA), and their environmental monitoring and audit (EM&A) Manuals (original EM&A Manuals), for the Project were approved by Environmental Protection Department (EPD) in October 2009.
- 1.1.3 EPD subsequently issued the Environmental Permit (EP) for HKBCF in November 2009 (EP-353/2009) and the Variation of Environmental Permit (VEP) in June 2010 (EP-353/2009/A), November 2010 (EP-353/2009/B), November 2011 (EP-353/2009/C), March 2012 (EP-353/2009/D), October 2012 (EP-353/2009/E), April 2013 (EP-353/2009/F) and August 2013 (EP-353/2009/G). Similarly, EPD issued the Environmental Permit (EP) for TMCLKL in November 2009 (EP-354/2009) and the Variation of Environmental Permit (VEP) in December 2010 (EP-354/2009/A) and January 2014 (EP-354/2009/B).
- 1.1.4 The Project is a designated project and is governed by the current permits for the Project, i.e. the amended EPs issued on 6 August 2013 (EP-353/2009/G) and 28 January 2014 (EP-354/2009/B) (for TMCLKL Southern Landfall Reclamation only).
- 1.1.5 A Project Specific EM&A Manual, which included all project-relation contents from the original EM&A Manuals for the Project, was issued in May 2012.
- 1.1.6 Ove Arup & Partners Hong Kong Limited (Arup) was appointed by Highways Department (HyD) as the consultants for the design and construction assignment for the Project’s reclamation works (i.e. the Engineer for the Project).
- 1.1.7 China Harbour Engineering Company Limited (CHEC) was awarded by HyD as the Contractor to undertake the construction work of the Project.
- 1.1.8 ENVIRON Hong Kong Ltd. was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO) for the Project.
- 1.1.9 AECOM Asia Co. Ltd. (AECOM) was appointed by CHEC to undertake the role of Environmental Team for the Project for carrying out the EM&A works.
- 1.1.10 The construction phase of the Project under the EPs was commenced on 12 March 2012 and will be tentatively completed by early Year 2016.
- 1.1.11 According to the Project Specific EM&A Manual, there is a need of an EM&A programme including air quality, noise, water quality and dolphin monitoring and environmental site inspections. The EM&A programme of the Project commenced on 12 March 2012.

1.2 Scope of Report

- 1.2.1 This is the twenty-seventh monthly EM&A Report under the Contract No. HY/2010/02 Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities – Reclamation Works. This report presents a summary of the environmental monitoring and audit works, list of activities and mitigation measures proposed by the ET for the Project in May 2014.

1.3 Project Organization

1.3.1 The project organization structure is shown in Appendix A. The key personnel contact names and numbers are summarized in Table 1.1.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name	Telephone	Fax
Engineer's Representative (ER) (Ove Arup & Partners Hong Kong Limited)	Chief Resident Engineer	Roger Marechal	3698 5700	2698 5999
IEC / ENPO (ENVIRON Hong Kong Limited)	Independent Environmental Checker	Raymond Dai	3465 2888	3465 2899
	Environmental Project Office Leader	Y. H. Hui	3465 2868	3465 2899
Contractor (China Harbour Engineering Company Limited)	Environmental Officer	Richard Ng	36932253	2578 0413
	24-hour Hotline	Alan C.C. Yeung	9448 0325	--
ET (AECOM Asia Company Limited)	ET Leader	Echo Leong	3922 9280	2317 7609

1.4 Summary of Construction Works

1.4.1 The construction phase of the Project under the EP commenced on 12 March 2012.

1.4.2 As informed by the Contractor, details of the major works carried out in this reporting period are listed below:-

Marine-based Works

- Connecting arc cell installation
- Laying geo-textile
- Sand blanket laying
- Sand filling
- Maintenance of silt curtain & silt screen at sea water intake of HKIA
- Stone column installation
- Band drain installation
- Backfill cellular structure
- Geotechnical Instrumentation works
- Construction of temporary seawall
- Portion D Construction of Access to Portion A
- Surcharge laying
- Construction of temporary pier at Portion A
- Precast Yard setup
- Seawall blocks for temporary construction
- Vibro-compaction on surcharge
- Capping Beams structures

- Construction of Conveyors for public fill
- Temporary bridge at Portion D

Land-based Works

- Maintenance works of Site Office at Works Area WA2
- Maintenance works of Public Works Regional Laboratory at Works Area WA3
- Geo-textile fabrication at Works Area WA2
- Installed sand bag at Works Area WA2
- Maintenance of Temporary Marine Access at Works Area WA2

1.4.3 The 3-month rolling construction programme of the Project is shown in Appendix B.

1.4.4 The general layout plan of the Project site showing the detailed works areas is shown in Figure 1.

1.4.5 The environmental mitigation measures implementation schedule are presented in Appendix C.

1.5 Summary of EM&A Programme Requirements

1.5.1 The EM&A programme required environmental monitoring for air quality, noise, water quality, marine ecology and environmental site inspections for air quality, noise, water quality, waste management, marine ecology, and landscape and visual impact. The EM&A requirements for each parameter described in the following sections include:-

- All monitoring parameters;
- Monitoring schedules for the reporting month and forthcoming month;
- Action and Limit levels for all environmental parameters;
- Event / Action Plan;
- Environmental mitigation measures, as recommended in the Project EIA reports; and
- Environmental requirement in contract documents.

2 AIR QUALITY MONITORING

2.1 Monitoring Requirements

2.1.1 In accordance with the Project Specific EM&A Manual, baseline 1-hour and 24-hour Total Suspended Particulates (TSP) levels at 4 air quality monitoring stations were established. Impact 1-hour TSP monitoring was conducted for at least three times every 6 days, while impact 24-hour TSP monitoring was carried out for at least once every 6 days. The Action and Limit level of the air quality monitoring is provided in Appendix D.

2.2 Monitoring Equipment

2.2.1 24-hour TSP air quality monitoring was performed using High Volume Sampler (HVS) located at each designated monitoring station. The HVS meets all the requirements of the Project Specific EM&A Manual. Portable direct reading dust meters were used to carry out the 1-hour TSP monitoring. Brand and model of the equipment is given in Table 2.1.

Table 2.1 Air Quality Monitoring Equipment

Equipment	Brand and Model
Portable direct reading dust meter (1-hour TSP)	Sibata Digital Dust Monitor (Model No. LD-3 and LD-3B)
High Volume Sampler (24-hour TSP)	Tisch Environmental Mass Flow Controlled Total Suspended Particulate (TSP) High Volume Air Sampler (Model No. TE-5170)

2.3 Monitoring Locations

2.3.1 Monitoring locations AMS2 and AMS7 were set up at the proposed locations in accordance with Project Specific EM&A Manual. For AMS6 (Dragonair/CNAC (Group) Building), permission on setting up and carrying out impact monitoring works was sought, however, access to the premise has not been granted yet on this report issuing date. For monitoring location AMS3 (Ho Yu College), as proposed in the Project Specific EM&A Manual, approval for carrying out impact monitoring could not be obtained from the principal of the school. Permission on setting up and carrying out impact monitoring works at nearby sensitive receivers, like Caribbean Coast and Coastal Skyline, was also sought. However, approvals for carrying out impact monitoring works within their premises were not obtained. Impact air quality monitoring was conducted at site boundary of the site office area in Works Area WA2 (AMS3B) respectively. Same baseline and Action Level for air quality, as derived from the baseline monitoring data recorded at Ho Yu College, was adopted for this alternative air quality location.

2.3.2 Reference is made to ET’s proposal of the omission of air monitoring station (AMS 6) dated on 1 November 2012 and EPD’s letter dated on 19 November 2012 regarding the conditional approval of the proposed omission of air monitoring station (AMS 6) for Contract No. HY/2010/02. The aforesaid omission of Monitoring Station AMS6 is effective since 19 November 2012.

2.3.3 Figure 2 shows the locations of monitoring stations. Table 2.2 describes the details of the monitoring stations.

Table 2.2 Locations of Impact Air Quality Monitoring Stations

Monitoring Station	Location	Description
AMS2	Tung Chung Development Pier	Rooftop of the premise
AMS3B	Site Boundary of Site Office Area at Works Area WA2	On ground at the area boundary
AMS6*	Dragonair/CNAC (Group) Building	On ground at boundary of the premise
AMS7	Hong Kong SkyCity Marriott Hotel	On ground at boundary of the premise

*Remarks: Reference is made to EPD conditional approval of the omission of air monitoring station (AMS 6) for the project. The omission will be effective on 19 November 2012.

2.4 Monitoring Parameters, Frequency and Duration

2.4.1 Table 2.3 summarizes the monitoring parameters, frequency and duration of impact TSP monitoring.

Table 2.3 Air Quality Monitoring Parameters, Frequency and Duration

Parameter	Frequency and Duration
1-hour TSP	Three times every 6 days while the highest dust impact was expected
24-hour TSP	Once every 6 days

2.5 Monitoring Methodology

2.5.1 24-hour TSP Monitoring

- (a) The HVS was installed in the vicinity of the air sensitive receivers. The following criteria were considered in the installation of the HVS.
- (i) A horizontal platform with appropriate support to secure the sampler against gusty wind was provided.
 - (ii) No two samplers should be placed less than 2 meters apart.
 - (iii) The distance between the HVS and any obstacles, such as buildings, was at least twice the height that the obstacle protrudes above the HVS.
 - (iv) A minimum of 2 meters separation from walls, parapets and penthouse for rooftop sampler.
 - (v) A minimum of 2 meters separation from any supporting structure, measured horizontally is required.
 - (vi) No furnace or incinerator flues nearby.
 - (vii) Airflow around the sampler was unrestricted.
 - (viii) Permission was obtained to set up the samplers and access to the monitoring stations.
 - (ix) A secured supply of electricity was obtained to operate the samplers.
 - (x) The sampler was located more than 20 meters from any dripline.
 - (xi) Any wire fence and gate, required to protect the sampler, did not obstruct the monitoring process.
 - (xii) Flow control accuracy was kept within $\pm 2.5\%$ deviation over 24-hour sampling period.
- (b) Preparation of Filter Papers
- (i) Glass fibre filters, G810 were labelled and sufficient filters that were clean and without pinholes were selected.
 - (ii) All filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25 °C and not variable by more than ± 3 °C; the relative humidity (RH) was < 50% and not variable by more than $\pm 5\%$. A convenient working RH was 40%.

- (iii) All filter papers were prepared and analysed by ALS Technichem (HK) Pty Ltd., which is a HOKLAS accredited laboratory and has comprehensive quality assurance and quality control programmes.
- (c) Field Monitoring
- (i) The power supply was checked to ensure the HVS works properly.
 - (ii) The filter holder and the area surrounding the filter were cleaned.
 - (iii) The filter holder was removed by loosening the four bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully.
 - (iv) The filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter.
 - (v) The swing bolts were fastened to hold the filter holder down to the frame. The pressure applied was sufficient to avoid air leakage at the edges.
 - (vi) Then the shelter lid was closed and was secured with the aluminum strip.
 - (vii) The HVS was warmed-up for about 5 minutes to establish run-temperature conditions.
 - (viii) A new flow rate record sheet was set into the flow recorder.
 - (ix) On site temperature and atmospheric pressure readings were taken and the flow rate of the HVS was checked and adjusted at around 1.1 m³/min, and complied with the range specified in the updated EM&A Manual (i.e. 0.6-1.7 m³/min).
 - (x) The programmable digital timer was set for a sampling period of 24 hrs, and the starting time, weather condition and the filter number were recorded.
 - (xi) The initial elapsed time was recorded.
 - (xii) At the end of sampling, on site temperature and atmospheric pressure readings were taken and the final flow rate of the HVS was checked and recorded.
 - (xiii) The final elapsed time was recorded.
 - (xiv) The sampled filter was removed carefully and folded in half length so that only surfaces with collected particulate matter were in contact.
 - (xv) It was then placed in a clean plastic envelope and sealed.
 - (xvi) All monitoring information was recorded on a standard data sheet.
 - (xvii) Filters were then sent to ALS Technichem (HK) Pty Ltd. for analysis.
- (d) Maintenance and Calibration
- (i) The HVS and its accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
 - (ii) 5-point calibration of the HVS was conducted using TE-5025A Calibration Kit prior to the commencement of baseline monitoring. Bi-monthly 5-point calibration of the HVS will be carried out during impact monitoring.
 - (iii) Calibration certificate of the HVSs are provided in Appendix E.

2.5.2 1-hour TSP Monitoring

(a) Measuring Procedures

The measuring procedures of the 1-hour dust meter were in accordance with the Manufacturer's Instruction Manual as follows:-

- (i) Turn the power on.
- (ii) Close the air collecting opening cover.
- (iii) Push the "TIME SETTING" switch to [BG].
- (iv) Push "START/STOP" switch to perform background measurement for 6 seconds.
- (v) Turn the knob at SENS ADJ position to insert the light scattering plate.
- (vi) Leave the equipment for 1 minute upon "SPAN CHECK" is indicated in the display.
- (vii) Push "START/STOP" switch to perform automatic sensitivity adjustment. This measurement takes 1 minute.
- (viii) Pull out the knob and return it to MEASURE position.
- (ix) Push the "TIME SETTING" switch the time set in the display to 3 hours.
- (x) Lower down the air collection opening cover.
- (xi) Push "START/STOP" switch to start measurement.

(b) Maintenance and Calibration

- (i) The 1-hour TSP meter was calibrated at 1-year intervals against a continuous particulate TEOM Monitor, Series 1400ab. Calibration certificates of the Laser Dust Monitors are provided in Appendix E.
- (ii) 1-hour validation checking of the TSP meter against HVS is carried out on half-year basis at the air quality monitoring locations.

2.6 Monitoring Schedule for the Reporting Month

2.6.1 The schedule for air quality monitoring in May 2014 is provided in Appendix F.

2.7 Results and Observations

2.7.1 The monitoring results for 1-hour TSP and 24-hour TSP are summarized in Table 2.4 and 2.5 respectively. Detailed impact air quality monitoring results are presented in Appendix G.

Table 2.4 Summary of 1-hour TSP Monitoring Results in the Reporting Period

	Average ($\mu\text{g}/\text{m}^3$)	Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
AMS2	80	73 – 84	374	500
AMS3B	80	71 – 84	368	500
AMS7	80	75 – 84	370	500

Table 2.5 Summary of 24-hour TSP Monitoring Results in the Reporting Period

	Average ($\mu\text{g}/\text{m}^3$)	Range ($\mu\text{g}/\text{m}^3$)	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
AMS2	32	18 – 48	176	260
AMS3B	38	16 – 86	167	260
AMS7	43	20 – 64	183	260

2.7.2 All 1-Hour TSP and 24Hr TSP results were below the Action and Limit Level in the reporting month.

2.7.3 The event action plan is annexed in Appendix L.

2.7.4 Meteorological information collected from the wind station during the monitoring periods on the monitoring dates, as shown in Figure 2, including wind speed and wind direction, is annexed in Appendix H.

3 NOISE MONITORING

3.1 Monitoring Requirements

3.1.1 In accordance with the Project Specific EM&A Manual, impact noise monitoring was conducted for at least once per week during the construction phase of the Project. The Action and Limit level of the noise monitoring is provided in Appendix D.

3.2 Monitoring Equipment

3.2.1 Noise monitoring was performed using sound level meter at each designated monitoring station. The sound level meters deployed comply with the International Electrotechnical Commission Publications (IEC) 651:1979 (Type 1) and 804:1985 (Type 1) specifications. Acoustic calibrator was deployed to check the sound level meters at a known sound pressure level. Brand and model of the equipment is given in Table 3.1.

Table 3.1 Noise Monitoring Equipment

Equipment	Brand and Model
Integrated Sound Level Meter	Rion NL-31 & B&K2238
Acoustic Calibrator	Rion NC-73

3.3 Monitoring Locations

3.3.1 Monitoring locations NMS2 was set up at the proposed locations in accordance with Project Specific EM&A Manual. However, for monitoring location NMS3 (Ho Yu College), as proposed in the Project Specific EM&A Manual, approval for carrying out impact monitoring could not be obtained from the principal of the school. Permission on setting up and carrying out impact monitoring works at nearby sensitive receivers, like Caribbean Coast and Coastal Skyline, was also sought. However, approvals for carrying out impact monitoring works within their premises were not obtained. Impact noise monitoring was conducted at site boundary of the site office area in Works Area WA2 (NMS3B) respectively. Same baseline noise level (as derived from the baseline monitoring data recorded at Ho Yu College) and Limit Level were adopted for this alternative noise monitoring location.

3.3.2 Figure 2 shows the locations of the monitoring stations. Table 3.2 describes the details of the monitoring stations.

Table 3.2 Locations of Impact Noise Monitoring Stations

Monitoring Station	Location	Description
NMS2	Seaview Crescent Tower 1	Free-field on the rooftop of the premise
NMS3B	Site Boundary of Site Office Area at Works Area WA2	Free-field on ground at the area boundary.

3.4 Monitoring Parameters, Frequency and Duration

3.4.1 Table 3.3 summarizes the monitoring parameters, frequency and duration of impact noise monitoring.

Table 3.3 Noise Monitoring Parameters, Frequency and Duration

Parameter	Frequency and Duration
30-mins measurement at each monitoring station between 0700 and 1900 on normal weekdays (Monday to Saturday). L_{eq} , L_{10} and L_{90} would be recorded.	At least once per week

3.5 Monitoring Methodology

3.5.1 Monitoring Procedure

- (a) The sound level meter was set on a tripod at a height of 1.2 m above the ground for free-field measurements at NMS2. A correction of +3 dB(A) shall be made to the free field measurements.
- (b) All measurement at NMS3A were free field measurements in the reporting month at NMS3A. A correction of +3 dB(A) shall be made to the free field measurements.
- (c) The battery condition was checked to ensure the correct functioning of the meter.
- (d) Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:-
 - (i) frequency weighting: A
 - (ii) time weighting: Fast
 - (iii) time measurement: $L_{eq(30\text{-minutes})}$ during non-restricted hours i.e. 07:00 – 1900 on normal weekdays.
- (e) Prior to and after each noise measurement, the meter was calibrated using the acoustic calibrator for 94dB(A) at 1000 Hz. If the difference in the calibration level before and after measurement was more than 1 dB(A), the measurement would be considered invalid and repeat of noise measurement would be required after re-calibration or repair of the equipment.
- (f) During the monitoring period, the L_{eq} , L_{10} and L_{90} were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- (g) Noise measurement was paused during periods of high intrusive noise (e.g. dog barking, helicopter noise) if possible. Observations were recorded when intrusive noise was unavoidable.
- (h) Noise monitoring was cancelled in the presence of fog, rain, wind with a steady speed exceeding 5m/s, or wind with gusts exceeding 10m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.5.2 Maintenance and Calibration

- (a) The microphone head of the sound level meter was cleaned with soft cloth at regular intervals.
- (b) The meter and calibrator were sent to the supplier or HOKLAS laboratory to check and calibrate at yearly intervals.
- (c) Calibration certificates of the sound level meters and acoustic calibrators are provided in Appendix E.

3.6 Monitoring Schedule for the Reporting Month

3.6.1 The schedule for construction noise monitoring in May 2014 is provided in Appendix F.

3.7 Monitoring Results

3.7.1 The monitoring results for construction noise are summarized in Table 3.4 and the monitoring data is provided in Appendix I.

Table 3.4 Summary of Construction Noise Monitoring Results in the Reporting Period

	Average, dB(A), $L_{eq} (30 \text{ mins})$	Range, dB(A), $L_{eq} (30 \text{ mins})$	Limit Level, dB(A), $L_{eq} (30 \text{ mins})$
NMS2	66	65 – 67*	75
NMS3B	65	64 – 70*	70/65^

*+3dB(A) Façade correction included

^ Daytime noise Limit Level of 70 dB(A) applies to education institutions, while 65dB(A) applies during school examination period.

3.7.2 No Action or Limit Level Exceedance of construction noise was recorded in the reporting month.

3.7.3 Major noise sources during the noise monitoring included construction activities of the Project, construction activities by other contracts and nearby traffic noise.

3.7.4 The event action plan is annexed in Appendix L.

4 WATER QUALITY MONITORING

4.1 Monitoring Requirements

4.1.1 Impact water quality monitoring was carried out to ensure that any deterioration of water quality was detected, and that timely action was taken to rectify the situation. For impact water quality monitoring, measurements were taken in accordance with the Project Specific EM&A Manual. Appendix D shows the established Action/Limit Levels for the environmental monitoring works.

4.2 Monitoring Equipment

4.2.1 Table 4.1 summarises the equipment used in the impact water quality monitoring programme.

Table 4.1 Water Quality Monitoring Equipment

Equipment	Brand and Model
Dissolved Oxygen (DO) and Temperature Meter, Salinity Meter and Turbidimeter	YSI Model 6820
pH Meter	YSI Model 6820 or Thermo Orion 230A+
Positioning Equipment	JRC DGPS 224 Model JLR-4341 with J-NAV 500 Model NWZ4551
Water Depth Detector	Eagle Cuda-168
Water Sampler	Kahlsio Water Sampler (Vertical) 2.2 L with messenger

4.3 Monitoring Parameters, Frequency and Duration

4.3.1 Table 4.2 summarises the monitoring parameters, frequency and monitoring depths of impact water quality monitoring as required in the Project Specific EM&A Manual.

Table 4.2 Impact Water Quality Monitoring Parameters and Frequency

Monitoring Stations	Parameter, unit	Frequency	No. of depth
<p><i>Impact Stations:</i> IS5, IS(Mf)6, IS7, IS8, IS(Mf)9, IS10, IS(Mf)11, IS(Mf)16, IS17</p> <p><i>Control/Far Field Stations:</i> CS(Mf)3, CS(Mf)5, CS4, CS6, CSA</p> <p><i>Sensitive Receiver Stations:</i> SR3-SR7, SR10A&SR10B</p>	<ul style="list-style-type: none"> • Depth, m • Temperature, °C • Salinity, ppt • Dissolved Oxygen (DO), mg/L • DO Saturation, % • Turbidity, NTU • pH • Suspended Solids (SS), mg/L 	<p>Three times per week during mid-ebb and mid-flood tides (within ± 1.75 hour of the predicted time)</p>	<p>3 (1 m below water surface, mid-depth and 1 m above sea bed, except where the water depth is less than 6 m, in which case the mid-depth station may be omitted. Should the water depth be less than 3 m, only the mid-depth station will be monitored).</p>

4.4 Monitoring Locations

- 4.4.1 In accordance with the Project Specific EM&A Manual, twenty-one stations (9 Impact Stations, 7 Sensitive Receiver Stations and 5 Control/Far Field Stations) were designated for impact water quality monitoring. The nine Impact Stations (IS) were chosen on the basis of their proximity to the reclamation and thus the greatest potential for water quality impacts, the seven Sensitive Receiver Stations (SR) were chosen as they are close to the key sensitive receives and the five Control/ Far Field Stations (CS) were chosen to facilitate comparison of the water quality of the IS stations with less influence by the Project/ ambient water quality conditions.
- 4.4.2 Due to safety concern and topographical condition of the original locations of SR4 and SR10B, alternative impact water quality monitoring stations, naming as SR4 (N) and SR10B (N), were adopted, which are situated in vicinity of the original impact water quality monitoring stations (SR4 and SR10B) and could be reachable.
- 4.4.3 Due to the perimeter silt curtain was temporary rearranged to facilitate the safe anchorage of the construction barges/vessels and the original monitoring station IS17 was relocated to alternative impact water quality monitoring station IS17(N).
- 4.4.4 Same baseline and Action Level for water quality, as derived from the baseline monitoring data recorded, were adopted for these alternative impact water quality monitoring stations.
- 4.4.5 The locations of these monitoring stations are summarized in Table 4.3 and depicted in Figure 3.

Table 4.3 Impact Water Quality Monitoring Stations

Station	Description	East	North
IS5	Impact Station (Close to HKBCF construction site)	811579	817106
IS(Mf)6	Impact Station (Close to HKBCF construction site)	812101	817873
IS7	Impact Station (Close to HKBCF construction site)	812244	818777
IS8	Impact Station (Close to HKBCF construction site)	814251	818412
IS(Mf)9	Impact Station (Close to HKBCF construction site)	813273	818850
IS10	Impact Station (Close to HKBCF construction site)	812577	820670
IS(Mf)11	Impact Station (Close to HKBCF construction site)	813562	820716
IS(Mf)16	Impact Station (Close to HKBCF construction site)	814328	819497
IS17(N)	Impact Station (Close to HKBCF construction site)	814767	820391
SR3	Sensitive receivers (San Tau SSSI)	810525	816456
SR4(N)	Sensitive receivers (Tai Ho)	814705	817859
SR5	Sensitive receivers (Artificial Reef in NE Airport)	811489	820455
SR6	Sensitive receivers (Sha Chau and Lung Kwu Chau Marine Park)	805837	821818
SR7	Sensitive receivers (Tai Mo Do)	814293	821431
SR10A	Sensitive receivers (Ma Wan FCZ)1	823741	823495
SR10B(N)	Sensitive receivers (Ma Wan FCZ)2	823683	823187
CS(Mf)3	Control Station	809989	821117
CS(Mf)5	Control Station	817990	821129
CS4	Control Station	810025	824004
CS6	Control Station	817028	823992
CSA	Control Station	818103	823064

4.5 Monitoring Methodology

4.5.1 Instrumentation

- (a) The in-situ water quality parameters, viz. dissolved oxygen, temperature, salinity, turbidity and pH, were measured by multi-parameter meters (i.e. Model YSI 6820 CE-C-M-Y) and pH meter (i.e. Thermo Orion 230A+) respectively.

4.5.2 Operating/Analytical Procedures

- (a) Digital Differential Global Positioning Systems (DGPS) were used to ensure that the correct location was selected prior to sample collection.
- (b) Portable, battery-operated echo sounders were used for the determination of water depth at each designated monitoring station.
- (c) All in-situ measurements were taken at 3 water depths, 1 m below water surface, mid-depth and 1 m above sea bed, except where the water depth was less than 6 m, in which case the mid-depth station was omitted. Should the water depth be less than 3 m, only the mid-depth station was monitored.
- (d) At each measurement/sampling depth, two consecutive in-situ monitoring (DO concentration and saturation, temperature, turbidity, pH, salinity) and water sample for SS. The probes were retrieved out of the water after the first measurement and then re-deployed for the second measurement. Where the difference in the value between the first and second readings of DO or turbidity parameters was more than 25% of the value of the first reading, the reading was discarded and further readings were taken.
- (e) Duplicate samples from each independent sampling event were collected for SS measurement. Water samples were collected using the water samplers and the samples were stored in high-density polythene bottles. Water samples collected were well-mixed in the water sampler prior to pre-rinsing and transferring to sample bottles. Sample bottles were pre-rinsed with the same water samples. The sample bottles were then be packed in cool-boxes (cooled at 4°C without being frozen), and delivered to ALS Technichem (HK) Pty Ltd. for the analysis of suspended solids concentrations. The laboratory determination work would be started within 24 hours after collection of the water samples. ALS Technichem (HK) Pty Ltd. is a HOKLAS accredited laboratory and has comprehensive quality assurance and quality control programmes. For QA/QC procedures, one duplicate samples of every batch of 20 samples was analyzed.
- (f) The analysis method and reporting and detection limit for SS is shown in Table 4.4.

Table 4.4 Laboratory Analysis for Suspended Solids

Parameters	Instrumentation	Analytical Method	Reporting Limit	Detection Limit
Suspended Solid (SS)	Weighting	APHA 2540-D	0.5mg/L	0.5mg/L

- (g) Other relevant data were recorded, including monitoring location / position, time, water depth, tidal stages, weather conditions and any special phenomena or work underway at the construction site in the field log sheet for information.

4.5.3 Maintenance and Calibration

- (a) All in situ monitoring instruments would be calibrated and calibrated by ALS Technichem (HK) Pty Ltd. before use and at 3-monthly intervals throughout all stages of the water quality monitoring programme. Calibration details are provided in Appendix E.
- (b) The dissolved oxygen probe of YSI 6820 was calibrated by wet bulb method. Before the calibration routine, the sensor for dissolved oxygen was thermally equilibrated in water-saturated air. Calibration cup is served as a calibration chamber and it was loosened from airtight condition before it is used for the calibration. Calibration at ALS Technichem (HK) Pty Ltd. was carried out once every three months in a water sample with a known concentration of dissolved oxygen. The sensor was immersed in the water and after thermal equilibration, the known mg/L value was keyed in and the calibration was carried out automatically.
- (c) The turbidity probe of YSI 6820 is calibrated two times a month. A zero check in distilled water was performed with the turbidity probe of YSI 6820 once per monitoring day. The probe will be calibrated with a solution of known NTU at ALS Technichem (HK) Pty Ltd. once every three months.

4.6 Monitoring Schedule for the Reporting Month

- 4.6.1 The schedule for impact water quality monitoring in May 2014 is provided in Appendix F.

4.7 Results and Observations

- 4.7.1 Impact water quality monitoring results and graphical presentations are provided in Appendix J.
- 4.7.2 For impact water quality monitoring, no exceedance was recorded at all monitoring stations in the reporting period.

Table 4.5 Summary of Water Quality Exceedances

Station	Exceedance Level	DO (S&M)		DO (Bottom)		Turbidity		SS		Total	
		Ebb	Flood	Ebb	Flood	Ebb	Flood	Ebb	Flood	Ebb	Flood
IS5	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS(Mf)6	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS7	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS8	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS(Mf)9	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS10	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS(Mf)11	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS(Mf)16	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
IS17	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR3	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR4(N)	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR5	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR6	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR7	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR10A	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
SR10B (N)	Action	0	0	0	0	0	0	0	0	0	0
	Limit	0	0	0	0	0	0	0	0	0	0
Total	Action	0	0	0	0	0	0	0	0	0	
	Limit	0	0	0	0	0	0	0	0	0	

Note: S: Surface; and
 M: Mid-depth.

4.7.3 The event action plan is annexed in Appendix L.

5 DOLPHIN MONITORING

5.1 Monitoring Requirements

- 5.1.1 Vessel based surveys for the Chinese White Dolphin (CWD), *Sousa chinensis*, are to be conducted by a dedicated team comprising a qualified marine mammal ecologist and experienced marine mammal observers (MMOs). The purpose of the surveys are to evaluate the impact of the HKCBF reclamation and, if deemed detrimental, to take appropriate action as per the EM&A manual.
- 5.1.2 This 'Impact Monitoring' follows several months of 'Baseline Monitoring' so similar survey methodologies have been adopted to facilitate comparisons between datasets. Further, the data collected are compatible with, and are available for, incorporation into the data set managed by the Agriculture, Fisheries and Conservation Department (AFCD) as part of Hong Kong's long term Marine Mammal Monitoring Programme.

5.2 Monitoring Equipment

- 5.2.1 Table 5.1 summarises the equipment used for the impact dolphin monitoring.

Table 5.1 Dolphin Monitoring Equipment

Equipment	Model
Commercially licensed motor vessel	15m in length with a 4.5m viewing platform
Global Positioning System (GPS) x2	Integrated into T7000 Garmin GPS Map 78C
Computers (T7000 Tablet, Intel Atom)	Windows 7/MSO 13 Logger
Camera	Nikon D90 300m 2.8D fixed focus Nikon D90 20-400m zoom lens
Laser Rangefinder	Infinitor LRF1000/ Kings 950
Marine Binocular x3	Nexus 7 x 50 marine binocular with compass and reticules Fujinon 7 x 50 marine binocular with compass and reticules

5.3 Monitoring Frequency and Conditions

- 5.3.1 Dolphin monitoring is conducted twice per month in each survey area.
- 5.3.2 Dolphin monitoring is conducted only when visibility is good (e.g., over 1km) and the sea condition is at a Beaufort Sea State of 4 or better.
- 5.3.3 When thunder storm, black rain or typhoon warnings are in force, all survey effort is stopped.

5.4 Monitoring Methodology and Location

- 5.4.1 The impact dolphin monitoring is vessel-based and combines line-transect and photo-ID methodology. The survey follows pre-set and fixed transect lines in the two areas defined by AFCD as:
- 5.4.2 Northeast Lantau survey area; and
- 5.4.3 Northwest Lantau survey area.
- 5.4.4 The co-ordinates for the transect lines and layout map have been provided by AFCD and are shown in Table 5.2 and Figure 4.

Table 5.2 Impact Dolphin Monitoring Line Transect Co-ordinates (Provided by AFCD)

ID	HK Grid System		Long Lat in WGS84	
	X	Y	Long	Lat
1	804671	814577	113.870308	22.269741
1	804671	831404	113.869975	22.421696
2	805475	815457	113.878087	22.277704
2	805477	826654	113.877896	22.378814
3	806464	819435	113.887615	22.313643
3	806464	822911	113.887550	22.345030
4	807518	819771	113.897833	22.316697
4	807518	829230	113.897663	22.402113
5	808504	820220	113.907397	22.320761
5	808504	828602	113.907252	22.396462
6	809490	820466	113.916965	22.323003
6	809490	825352	113.916884	22.367128
7	810499	820690	113.926752	22.325043
7	810499	824613	113.926688	22.360464
8	811508	820847	113.936539	22.326475
8	811508	824254	113.936486	22.357241
9	812516	820892	113.946329	22.326894
9	812516	824254	113.946279	22.357255
10*	813525	818270	113.956156	22.303225
10*	813525	824657	113.956065	22.360912
11	814556	818449	113.966160	22.304858
11	814556	820992	113.966125	22.327820
12	815542	818807	113.975726	22.308109
12	815542	824882	113.975647	22.362962
13	816506	819480	113.985072	22.314192
13	816506	824859	113.985005	22.362771
14	817537	820220	113.995070	22.320883
14	817537	824613	113.995018	22.360556
15	818568	820735	114.005071	22.325550
15	818568	824433	114.005030	22.358947
16	819532	821420	114.014420	22.331747
16	819532	824209	114.014390	22.356933
17	820451	822125	114.023333	22.338117
17	820451	823671	114.023317	22.352084
18	821504	822371	114.033556	22.340353
18	821504	823761	114.033544	22.352903
19	822513	823268	114.043340	22.348458
19	822513	824321	114.043331	22.357971
20	823477	823402	114.052695	22.349680
20	823477	824613	114.052686	22.360610
21	805476	827081	113.877878	22.382668
21	805476	830562	113.877811	22.414103
22	806464	824033	113.887520	22.355164
22	806464	829598	113.887416	22.405423
23	814559	821739	113.966142	22.334574
23	814559	824768	113.966101	22.361920

*Remark: Due to the presence of deployed silt curtain systems at the site boundaries of the Project, some of the transect lines shown in Figure 5 could not be fully surveyed during the regular survey. Transect 10 is reduced from 6.4km to approximately 3.6km in length due to the HKBCF construction site. Therefore the total transect length for both NEL and NWL combined is reduced to approximately 111km.

5.5 Monitoring Procedures

- 5.5.1 The study area incorporates 23 transects which are to be surveyed twice per month. Each survey day lasts approximately 9 hours.
- 5.5.2 The survey vessel departs from Tung Chung Development Pier, Tsing Yi Public Pier or the nearest safe and convenient pier.
- 5.5.3 When the vessel reaches the start of a transect line, “on effort” survey begins. Areas between transect lines and traveling to and from the study area are defined as “off effort”.
- 5.5.4 The transect line is surveyed at a speed of 6-8 knots (11-14 km/hr). For the sake of safety, the speed was sometimes a bit slower to avoid collision with other vessels. During some periods, tide and current flow in the survey areas exceeds 7 knots which can affect survey speed. There are a minimum of four marine mammal observers (MMOs) present on each survey, rotating through four positions, observers (2), data recorder (1) and ‘rest’ (1). Rotations occur every 30 minutes or at the end of dolphin encounters. The data recorder records effort, weather and sightings data directly onto the programme Logger and is not part of the observer team. The observers search with naked eye and binoculars between 90° and 270° abeam (bow being 0°).
- 5.5.5 When a group of dolphins is sighted, position, bearing and distance data are recorded immediately onto the computer and, after a short observation, an estimate made of group size. These parameters are linked to the time-GPS-ships data which are automatically stored in the programme Logger throughout the survey period. In this manner, information on heading, position, speed, weather, effort and sightings are stored in a format suitable for use with DISTANCE software for subsequent line transect analyses.
- 5.5.6 Once the vessel leaves the transect line, it is deemed to be “off effort”. The dolphins are approached with the purpose of taking high resolution pictures for proper photo-identification of individual CWD. Attempts to photograph all dolphins in the group are made. Both the left and right hand sides of the dorsal fin area of each dolphin in the group are photographed, if possible. On finishing photographing, the vessel will return to the transect line at the point of departure and “on effort” survey is resumed.
- 5.5.7 Sightings which are made while on the transect line are referred to as “on effort sightings”, while not on the actual transect line are referred to as an “opportunistic sightings” (e.g. another group of dolphins is sighted while travelling back to the transect line). Only “on effort sightings” can be used in analyses which require effort or rate quantification, e.g., encounter rate per 100km searched. This is also how “on effort sightings” are treated in the baseline report. “Opportunistic sightings” provide additional information on individual habitat use and population distribution and they are noted accordingly.
- 5.5.8 As time and GPS data are automatically logged throughout the survey and are linked to sightings data input, start and end times of encounters and deviation from the transect lines are recorded and can be subsequently reviewed.

5.6 Monitoring Schedule for the Reporting Month

- 5.6.1 The schedule for dolphin monitoring in May 2014 is provided in Appendix F.
- 5.6.2 Boat survey on 9 May 14 was cancelled due to predicted adverse weather and boat survey on 26 May 14 was rescheduled to 31 May 14
- 5.6.3 Two surveys covering both study areas were completed.

5.7 Results and Observations

- 5.7.1 Dolphin surveys were conducted on 8, 12, 27 and 31 May 2014. A total of 221.0 km of transect line was conducted under favourable conditions. The total length travelled was also 221.0km, please note that that some lines were shortened due to works and/or shipping traffic.

The effort summary and sightings data are shown in Tables 5.3 and 5.4, respectively. The survey efforts conducted in May 2014 are plotted in Figure 5a-b. For Table 5.3, only on-effort information is included. Transects conducted in all Beaufort Sea State are included. Compared to previous monthly reports, the whole number Beaufort Sea State scale is used so as to ease comparison with other dolphin monitoring reports.

Table 5.3 Impact Dolphin Monitoring Survey Effort Summary, Effort by Area and Beaufort Sea State

Survey	Date	Area	Beaufort	Effort (km)	Total Distance Travelled (km)
1	08/05/2014	NWL	1	26.5	63.0
	08/05/2014	NWL	2	36.5	
	12/05/2014	NWL	1	7.2	47.6
	12/05/2014	NWL	2	3.1	
	12/05/2014	NEL	1	16.3	
	12/05/2014	NEL	2	21	
2	27/05/2014	NWL	1	19.3	60.8
	27/05/2014	NWL	2	4.3	
	27/05/2014	NEL	1	27.4	
	27/05/2014	NEL	2	9.8	
	31/05/2014	NWL	1	12.4	49.6
	31/05/2014	NWL	2	37.2	
TOTAL in May 2014					221.0

*Remark: Surveys conduct under Beaufort Sea State 3 or below are considered as under favourable condition.

Table 5.4 Impact Dolphin Monitoring Survey Details May 2014

Date	Location	No. Sightings "on effort"	No. Sightings "opportunistic"
08/05/2014	NW L	0	0
	NEL	0	0
12/05/2014	NW L	0	0
	NEL	0	0
27/05/2014	NW L	0	0
	NEL	0	0
31/05/2014	NW L	1	2
	NEL	0	0
TOTAL in May 2014		1	2

Table 5.5 The Encounter Rate of Number of Dolphin Sightings & Total Number of Dolphins per Area[^]

Encounter Rate of Number of Dolphin Sightings (STG)[*]						
Date	NEL Track	NWL Track	NEL Sightings	NWL Sightings	NEL Encounter Rate	NWL Encounter Rate
8 & 12/05/2014	37.3 km	73.3 km	0	0	0	0
27 & 31/05/2014	37.2 km	73.2 km	0	1	0	1.4
Encounter Rate of Total Number of Dolphins (ANI)^{**}						
Date	NEL Track	NWL Track	NEL Dolphins	NWL Dolphins	NEL Encounter Rate	NWL Encounter Rate
8 & 12/05/2014	37.3 km	73.3 km	0	0	0	0
27 & 31/05/2014	37.2 km	73.2 km	0	3	0	4.1

* Encounter Rate of Number of Dolphin Sightings (STG) presents encounter rates in terms of groups per 100km.

** Encounter Rate of Total Number of Dolphins (ANI) presents encounter rates in terms of individuals per 100km. And the encounter rate is not corrected for individuals, calculation may represent double counting.

[^]The table is made only for reference to the quarterly STG & ANI, which were adopted for the Event & Action Plan.

- 5.7.2 A total of three sightings were made, two “opportunistic” and one “on effort”. All sightings were made on the 31st of May. A total of eighteen individuals were sighted from the two impact dolphin surveys in the reporting period. Sighting details are summarised and plotted in Appendix K and Figure 5c, respectively.
- 5.7.3 Behaviour: Of the three sightings, two groups were feeding and the third engaged in multiple activities which included milling and feeding. The locations of sighting with different behaviour are mapped in Figure 5d.
- 5.7.4 One (1) Limit Level Exceedance of dolphin monitoring was noted. The investigation is undergoing and the investigation results will be reported in the quarterly EM&A report (Mar 14 – May 14).
- 5.7.5 Photo ID analyses for April 2014 is presented in Appendix K.
- 5.7.6 There was one new individual (HZMB119) added to the catalogue in April 2014. Photo ID is included in Appendix K for reference.
- 5.7.7 Noteworthy Observation¹:
 - 5.7.6.1 When impact monitoring was conducted at the northern ends of transect lines 9 & 10, the view of the area was partially blocked by the working vessels and in water structures of TMCLKL Project. As the barges will move during the on-going works, it is considered that they will temporarily affect survey data collection, dolphin movement, dolphin habitat use and dolphin behaviour, whereas the fixed structures will continuously affect survey data collection, dolphin movement, dolphin habitat use and dolphin behaviour. One of the aims of the impact monitoring is to attempt to assess the degree of these effects.
 - 5.7.6.2 When impact monitoring was conducted at the southern ends of transect lines 1 & 2, the view of the area and the transect lines were partially blocked by the working vessels and in water structures of Hong Kong Links Road Project. As the barges will move during the on-going works, it is considered that they will temporarily affect survey protocol, survey data collection, dolphin movement, dolphin

¹ A noteworthy observation is to show that either the conduct of the surveys themselves is affected, i.e., the noted vessel or works impedes the progress or view of the survey platform. In addition, the vessel or construction works may be different or additional to that observed previously and further, are of such a nature that they are a likely to create an impact on the movement or behaviour of the subject of the impact survey, in this case, the dolphins.

habitat use and dolphin behaviour, whereas the fixed structures will continuously affect survey protocol, survey data collection, dolphin movement, dolphin habitat use and dolphin behaviour. One of the aims of the impact monitoring is to attempt to assess the degree of these effects.

- 5.7.6.3 The HKBCF Project affected lines 10 and 12 and the new projects noted previously were ongoing at the southern ends of lines 5 and 6.
- 5.7.6.4 The survey effort log notes the areas in which the visibility is limited or the survey is affected so that these can be accounted for in any subsequent analyses. Some of these obstructions will become permanent and some will be temporary as the HZMB is built and other projects progress. It is advised that the impact monitoring surveys should be completed as close to the predefined lines as possible (as per Figure 4 of this report).
- 5.7.6.5 In May 14, the impact survey vessel route shifted slightly to the east at the northern end of transect line 11 due to works at HKBCF. In future, the impact survey route will follow as closely as possible the predefined transect 11. According to the review provided by the dolphin specialist during the investigation in Jan 2014, the shift in the transect line will not affect the overall dolphin impact monitoring analyses.
- 5.7.8 The event action plan is annexed in Appendix L.

6 ENVIRONMENTAL SITE INSPECTION AND AUDIT

6.1 Site Inspection

6.1.1 Site Inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. In the reporting month, 5 site inspections were carried out on 2, 8, 15, 22 and 29 May 2014.

6.1.2 Oil stain was discovered near portion A on 21 May 2014. The source was identified as oil leakage from the flattop barge Luen Hung (聯興) 368 with approximately 50m² spread. As informed by the Contractor, the source of oil stain was from an oil drum toppled from the flattop barge. Following the spill response plan, relevant parties were informed of the incident and the Contractor used absorption booms to contain and remove the floating oil from water and material used for such was collected using disposal bags as part of the spill kits item. Such spillage incident was considered as project related. The Contractor was reminded to properly implement all the precautionary actions listed in the spill response plan to prevent similar incident in the future. No similar incident was recorded in the rest of the reporting month.

6.1.3 Particular observations during the site inspections are described below:

Air Quality

6.1.4 Exposed soil observed fully loaded on barge at near Portion D. The Contractor was reminded to provide dust control measures and keep the surface of all exposed soil wet and the Contractor was reminded to use suitable barge to store public fill to prevent potential runoff to the surrounding. (Reminder)

6.1.5 Exposed earth was observed at Portion A. The Contractor was reminded to provide dust control measures such as to treat the exposed earth by compaction. The Contractor provided dust control measures such as to treat the exposed earth by compaction. (Closed)

6.1.6 Stock pile of soil was observed on portion C2a. The Contractor was reminded to compact the soil/provide dust mitigation measures such watering to exposed stock pile of sand to prevent potential fugitive dust generation. (Reminded)

6.1.7 Fugitive dust was observed generated on site at Portion D. The Contractor provided dust suppression measures such a compaction and watering to exposed soil. The Contractor was reminded to review the effectiveness of the abovementioned mitigation measures and to review the need to provide enhancement on current measures. In addition, high pressure water jet was observed at site entrance at Portion D, Nonetheless, the Contractor was reminded to review the need to enhance the wheel washing facility to effectively prevent potential trail of mud outside site boundary cause by site vehicles. (Reminder)

Noise

6.1.8 Generator was observed without acoustic decoupling measures on barge 天駿 3. The Contractor was reminded to install acoustic decoupling measure prior to leaving Portion A. (Reminder)

Water Quality

6.1.9 Stockpile of soil was observed on barge AP3 at Portion D, the Contractor was reminded to provide measures to prevent potential runoff during rainstorm. (Reminder)

6.1.10 The Contractor was reminded that the chemical waste containers should be kept in good condition and free from damage or any other defects which may impair the performance of the containers. The Contractor removed the containers. (Closed)

6.1.11 Generator, drip tray and water pump were observed located too close to the water level in the reporting period, the Contractor was reminded place equipments at higher ground to prevent potential oil

spillage/runoff. The Contractor placed generator at higher ground to prevent potential oil spillage/runoff (Closed)

6.1.12 Water was observed accumulated inside drip tray at C2a near the blue conveyor belts and other areas. The Contractor was reminded to clear water inside drip tray at C2a near the blue conveyor belts. The Contractor cleared the water inside drip tray at C2a and other areas. (Closed)

6.1.13 Idle stone column installation plant was observed without localised silt curtain to fully enclose it. The Contractor was reminded to fully enclose the stone column installation works prior to stone column installation. (Reminder)

Chemical and Waste Management

6.1.14 Used band drains were observed stored on site at Portion A. The Contractor was reminded to regularly collect and dispose the used band drain materials. The Contractor cleared unwanted band drains regularly. Band drain material and general refuse were observed at the road side at Portion A. The Contractor cleared general refuse stored on site. Nonetheless, the Contractor was reminded to clear unwanted band drain and other general refuse stored on site regularly. (Reminder)

6.1.15 General refuse and disconnected silt curtain were observed next to cellular structure, at Portion A's waste collection point and on the way from Portion D to C2a. The Contractor was reminded to collect the refuse and the disconnected silt curtain presented in the water within and adjacent to the works site. The Contractor collected the refuse presented in the water within and adjacent to the works site. The Contractor was reminded to review the need to increase frequency to clear and dispose of the waste at waste collection point to avoid accumulation. (Reminder)

6.1.16 Stone and gravel were observed inside drip tray containing oil drums. The Contractor was reminded to relocate the drip tray with the oil drums to avoid the situation. The Contractor relocated the drip tray with the oil drums to avoid the situation. (Closed)

Landscape and Visual Impact

6.1.17 No relevant works was carried out in the reporting month.

Others

6.1.18 Rectifications of remaining identified items are undergoing by the Contractor. Follow-up inspections on the status on provision of mitigation measures will be conducted to ensure all identified items are mitigated properly.

6.2 Advice on the Solid and Liquid Waste Management Status

- 6.2.1 The Contractor had registered as a chemical waste producer for this Project. Receptacles were available for general refuse collection and sorting.
- 6.2.2 As advised by the Contractor, 1,181,416.8m³ of fill were imported for the Project use in the reporting period. 40kg of metals, 24kg of paper/cardboard packaging, 1,000kg of chemical waste, 91m³ of general refuse were generated and disposed of in the reporting period. Monthly summary of waste flow table is detailed in Appendix M.
- 6.2.3 The Contractor is advised to properly maintain on site C&D materials and wastes storage, collection, sorting and recording system, dispose of C&D materials and wastes at designated ground and maximize reuse / recycle of C&D materials and wastes. The Contractor is reminded to properly maintain the site tidiness and dispose of the wastes accumulated on site regularly and properly.
- 6.2.4 The Contractor is reminded that chemical waste should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labeling and Storage of Chemical Wastes.

6.3 Environmental Licenses and Permits

6.3.1 The environmental licenses and permits for the Project and valid in the reporting month is summarized in Table 6.1.

Table 6.1 Summary of Environmental Licensing and Permit Status

Statutory Reference	License/ Permit	License or Permit No.	Valid Period		License/ Permit Holder	Remarks
			From	To		
EIAO	Environmental Permit	EP-353/2009/G	06/08/2012	N/A	HyD	Hong Kong – Zhuhai – Macao Bridge Hong Kong Boundary Crossing Facilities
		EP-354/2009/B	28/01/2014	N/A		Tuen Mun – Chek Lap Kok Link (TMCLKL Southern Landfall Reclamation only)
APCO	NA notification	--	30/12/2011	--	CHEC	Works Area WA2 and WA3
APCO	NA notification	--	17/01/2012	--	CHEC	Works Area WA4
WDO	Chemical Waste Producer Registration	5213-951-C1186-21	30/3/2012	N/A	CHEC	Chemical waste produced in Contract HY/2010/02
WDO	Chemical Waste Producer Registration	5213-974-C3750-01	31/10/2012	--	CHEC	Registration as Chemical Waste Producer at To Kau Wan(WA4)
WDO	Chemical Waste Producer Registration	5213-839-C3750-02	13/09/2012	--	CHEC	Registration as Chemical Waste Producer at TKO 137(FB)
WDO	Billing Account for Disposal of Construction Waste	7014181	05/12/2011	N/A	CHEC	Waste disposal in Contract HY/2010/02
NCO	Construction Noise Permit	GW-RW0888-13	27/12/2013	26/06/2014	CHEC	Works Area WA4 in Contract HY/2010/02
NCO	Construction Noise Permit	GW-RS0211-14	11/03/2014	10/09/2014	CHEC	Reclamation Works in Contract HY/2010/02
NCO	Construction Noise Permit	GW-RS0490-14	22/05/2014	21/08/2014	CHEC	Reclamation Works in Contract HY/2010/02
NCO	Construction Noise Permit	GW-RE1345-13	31/12/2013	30/06/2014	CHEC	Section of TKO Fill Bank under Contract HY/2010/02

6.4 Implementation Status of Environmental Mitigation Measures

6.4.1 In response to the site audit findings, the Contractors carried out corrective actions.

6.4.2 A summary of the Implementation Schedule of Environmental Mitigation Measures (EMIS) is presented in Appendix C. Most of the necessary mitigation measures were implemented properly.

6.4.3 Training of marine travel route for marine vessels operator was given to relevant staff and relevant records were kept properly.

- 6.4.4 Regarding the implementation of dolphin monitoring and protection measures (i.e. implementation of Dolphin Watching Plan, Dolphin Exclusion Zone and Silt Curtain integrity Check), regular checking were conducted by the experienced MMOs within the works area to ensure no dolphin was trapped by the enclosed silt curtain systems. Any dolphin spotted within the enclosed silt curtain systems was reported and recorded. Relevant procedures were followed and measures were well implemented. Silt curtain systems were also inspected timely in accordance to the submitted plan. All inspection records were kept properly.
- 6.4.5 Acoustic decoupling measures on noisy plants on construction vessels were checked regularly and the Contractor was reminded to ensure provision of ongoing maintenance to noisy plants and to carry out improvement work once insufficient acoustic decoupling measures were found.
- 6.4.6 Frequency of watering per day on exposed soil was checked; with reference to the record provided by the Contract, watering was conducted at least 8 times per day on reclaimed land. The Contractor was reminded to ensure provision of watering of at least 8 times per day on all exposed soil within the Project site and associated works areas throughout the construction phase.

6.5 Summary of Exceedances of the Environmental Quality Performance Limit

- 6.5.1 All 1-Hour TSP and 24-hour TSP results were below the Action and Limit Level in the reporting month.
- 6.5.2 For construction noise, no exceedance was recorded at all monitoring stations in the reporting period.
- 6.5.3 For impact water quality monitoring, no exceedance was recorded at all monitoring stations in the reporting period.
- 6.5.4 One (1) Limit Level Exceedance of dolphin monitoring was noted. The investigation is undergoing and the investigation results will be reported in the quarterly EM&A report (Mar 14 – May 14).
- 6.5.5 Cumulative statistics on exceedance is provided in Appendix N.

6.6 Summary of Complaints, Notification of Summons and Successful Prosecutions

- 6.6.1 The Environmental Complaint Handling Procedure is annexed in Figure 6.
- 6.6.2 As informed by the Contractor on 7 May 14, a complaint was received by the Contractor on 17 April 14 concerning sand and dust emission from uncovered barges parking at the sea area off the Tuen Mun Ferry Pier.
- 6.6.2.1 As informed by the Contractor 7-10 trips of sand barges per week would stay at the concerned Area.
- 6.6.2.2 However, because no extra information was received for this complaint after the release of last investigation report, with referred to the available information; it is unable to conclude whether the complaint is related to this Contract because:
1. There is no sufficient information provided by the complainant to make sure that the concerned barges are related to this project.
 2. The sand barges at the construction site of the reclamation works were regularly checked and so far, all sand barges were observed equipped with watering equipments.
 3. Photo record below shows that watering equipment was used to keep the sand filling material wet.
- 6.6.2.3 Photo record shows that watering equipment was provided on pelican barge loaded with sand for watering of sand filling material to keep the sand material wet:



- 6.6.2.4 Nevertheless, the Contractor was reminded to continue to properly implement all dust mitigation measures.
- 6.6.2.5 The Contractor was advised to ensure to continue the provision of fugitive dust mitigation measures to barges loaded with filling material such as watering to sand filling material on sand barges to keep the surface of stockpile of filling material wet.
- 6.6.2.6 As informed by the Contractor, skipper of all working barges would further be reminded to beware and to pay particular attention to the issue concerning sand and dust emission from uncovered barges parking at the sea area off the Tuen Mun Ferry Pier.
- 6.6.3 As informed by the Contractor on 30 May 2014, an environmental complaint had been received on 28 May 2014. The complainant mentioned that waste such as earth and concrete were being felled into the sea everyday at the Hong Kong-Zhuhai-Macao Bridge at location where construction works are being conducted, causing pollution to the marine environment.
- 6.6.3.1 Site inspections were conducted and project documents were reviewed, please see the following for details of investigation actions and results:
- 6.6.3.2 Regular site inspection was conducted on 29 May 2014 and a follow up site inspection was conducted on 5 June 2014 at HKBCF Reclamation Works, waste such as concrete and earth were not observed being felled into the sea.
- 6.6.3.3 The waste flow record provided by the Contractor has been reviewed (please see attached), the waste flow record shows that waste described by the complainant (i.e. concrete or earth) were not generated by this Contract.
- 6.6.3.4 In addition, the construction programme provided by the Contractor (Please see construction program attached) has been reviewed and it is noted that concrete and earth were not used as marine fill for any on-going construction activities of this Contract in May 2014. Also, all filling works were conducted inside the designated work zone inside the site boundary of HKBCF Reclamation Works. Furthermore, impact water quality monitoring result of May 2014 has been reviewed and no impact water quality exceedance was recorded in May 2014, this indicates that the works carried by this Contract is unlikely to cause pollution to the marine environment.
- 6.6.3.5 As such, with referred to the available information, it is concluded that the complaint is unlikely to be related to this Contract.
- 6.6.3.6 Nevertheless, the Contractor was reminded to continue to properly implement all water quality mitigation measures and strictly follow the waste handling procedure according of this Contract.
- 6.6.4 No notification of summons and successful prosecutions was received in the reporting period.
- 6.6.5 Statistics on complaints, notifications of summons and successful prosecutions are summarized in Appendix N.

7 FUTURE KEY ISSUES

7.1 Construction Programme for the Coming Months

7.1.1 As informed by the Contractor, the major works for the Project in June 2014 and July 2014 will be *:-

Marine-based Works

- Marine-base
- Cellular structure installation
- Connecting arc cell installation
- Laying geo-textile
- Sand blanket laying
- Sand filling
- Maintenance of silt curtain & silt screen at sea water intake of HKIA
- Stone column installation
- Band drain installation
- Backfill cellular structure
- Geotechnical Instrumentation works
- Surcharge laying
- Vibro-compaction on surcharge
- Capping Beams structures
- Construction of temporary jetties for surcharge laying
- Temporary Watermain construction along access at Portion D

Land-based Works

- Maintenance works of Site Office at Works Area WA2
- Maintenance works of Public Works Regional Laboratory at Works Area WA3
- Maintenance of Temporary Marine Access at Works Area WA2

*Construction activities in Jun & Jul 14 will be changed subject to works progress.

7.2 Key Issues for the Coming Month

7.2.1 Key issues to be considered in the coming months:-

- Site runoff should be properly collected and treated prior to discharge;
- Minimize loss of sediment from filling works;
- Regular review and maintenance of silt curtain systems, drainage systems and desilting facilities;
- Exposed surfaces/soil stockpiles should be properly treated to avoid generation of silty surface runoff during rainstorm;
- Regular review and maintenance of wheel washing facilities provided at all site entrances/exits;
- Conduct regular inspection of various working machineries and vessels within works areas to avoid any dark smoke emission;
- Suppress dust generated from work processes with use of bagged cements, earth movements, excavation activities, exposed surfaces/soil stockpiles and haul road traffic;
- Quieter powered mechanical equipment should be used;
- Provision of proper and effective noise control measures for operating equipment and machinery on-site, such as erection of movable noise barriers or enclosure for noisy plants;
- Closely check and replace the sound insulation materials regularly;
- Better scheduling of construction works to minimize noise nuisance;
- Properly store and label oil drums and chemical containers placed on site;
- Proper chemicals, chemical wastes and wastes management;
- Maintenance works should be carried out within roofed, paved and confined areas;
- Collection and segregation of construction waste and general refuse on land and in the sea should be carried out properly and regularly; and
- Proper protection and regular inspection of existing trees, transplanted/retained trees.

7.3 Monitoring Schedule for the Coming Month

7.3.1 The tentative schedule for environmental monitoring in June 2014 is provided in Appendix F.

8 CONCLUSIONS AND RECOMMENDATIONS

8.1 Conclusions

- 8.1.1 The construction phase and EM&A programme of the Project commenced on 12 March 2012.
- 8.1.2 All 1-Hour TSP and 24-hour TSP results were below the Action and Limit Level in the reporting month.
- 8.1.3 For construction noise, no exceedance was recorded at all monitoring stations in the reporting period.
- 8.1.4 For impact water quality monitoring, no exceedance was recorded at all monitoring stations in the reporting period.
- 8.1.5 For dolphin monitoring, a total of three sightings were made, two “opportunistic” and one “on effort”. All sightings were made on the 31st of May. A total of eighteen individuals were sighted from the two impact dolphin surveys in the reporting period. Sighting details are summarised and plotted in Appendix K and Figure 5c, respectively.
- 8.1.6 Behaviour: Of the three sightings, two groups were feeding and the third engaged in multiple activities which included milling and feeding. The locations of sighting with different behaviour are mapped in Figure 5d.
- 8.1.7 One (1) Limit Level Exceedance of dolphin monitoring was noted. The investigation is undergoing and the investigation results will be reported in the quarterly EM&A report (Mar 14 – May 14).
- 8.1.8 Environmental site inspection was carried out 5 times in May 2014. Recommendations on remedial actions were given to the Contractors for the deficiencies identified during the site audits.
- 8.1.9 As informed by the Contractor on 7 May 14, a complaint was received by the Contractor on 17 April 14 concerning sand and dust emission from uncovered barges parking at the sea area off the Tuen Mun Ferry Pier. Investigation result shows that the complaint is unlikely to be related to this Contract.
- 8.1.10 As informed by the Contractor on 30 May 14, an environmental complaint had been received on 28 May 2014. The complainant mentioned that waste such as earth and concrete were being felled into the sea everyday at the Hong Kong-Zhuhai-Macao Bridge at location where construction works are being conducted, causing pollution to the marine environment. After investigation, it is concluded that the complaint is unlikely to be related to this Contract.
- 8.1.11 No notification of summons and successful prosecution was received in the reporting period.

8.2 Recommendations

8.2.1 According to the environmental site inspections performed in the reporting month, the following recommendations were provided:

Air Quality Impact

- All working plants and vessels on site should be regularly inspected and properly maintained to avoid dark smoke emission.
- All vehicles should be washed to remove any dusty materials before leaving the site.
- Haul roads should be sufficiently dampened to minimize fugitive dust generation.
- Wheel washing facilities should be properly maintained and reviewed to ensure properly functioning.
- Temporary exposed slopes and open stockpiles should be properly covered.
- Enclosure should be erected for cement debagging, batching and mixing operations.
- Water spraying should be provided to suppress fugitive dust for any dusty construction activity.

Construction Noise Impact

- Quieter powered mechanical equipment should be used as far as possible.
- Noisy operations should be oriented to a direction away from sensitive receivers as far as possible.
- Proper and effective noise control measures for operating equipment and machinery on-site should be provided, such as erection of movable noise barriers, enclosure for noisy plants or enhancement works to provide sufficient acoustic decoupling measure(s). Closely check and replace the sound insulation materials regularly
- Vessels and equipment operating should be checked regularly and properly maintained.
- Noise Emission Label (NEL) shall be affixed to the air compressor and hand-held breaker operating within works area.
- Acoustic decoupling measures should be properly implemented for all existing and incoming construction vessels with continuous and regularly checking to ensure effective implementation of acoustic decoupling measures.

Water Quality Impact

- Regular review and maintenance of silt curtain systems, drainage systems and desilting facilities in order to make sure they are functioning effectively.
- Construction of seawall should be completed as early as possible.
- Regular inspect and review the loading process from barges to avoid splashing of material.
- Silt, debris and leaves accumulated at public drains, wheel washing bays and perimeter u-channels and desilting facilities should be cleaned up regularly.
- Silty effluent should be treated/ desilted before discharged. Untreated effluent should be prevented from entering public drain channel.
- Proper drainage channels/bunds should be provided at the site boundaries to collect/intercept the surface run-off from works areas.
- Exposed slopes and stockpiles should be covered up properly during rainstorm.


Chemical and Waste Management

- All types of wastes, both on land and floating in the sea, should be collected and sorted properly and disposed of timely and properly. They should be properly stored in designated areas within works areas temporarily.
- All chemical containers, batteries and oil drums should be properly stored and labelled.
- All plants and vehicles on site should be properly maintained to prevent oil leakage. Proper measures, like drip trays and/or bundings, should be provided for retaining leaked oil/chemical from plants.
- All kinds of maintenance works should be carried out within roofed, paved and confined areas.
- All drain holes of the drip trays utilized within works areas should be properly plugged to avoid any oil and chemical waste leakage.
- Oil stains on soil surface, accumulated oil mixture and empty chemical containers should be cleared and disposed of as chemical waste.
- Regular review should be conducted for working barges and patrol boats to ensure sufficient measures and spill control kits were provided on working barges and patrol boats to avoid any spreading of leaked oil/chemicals.

Landscape and Visual Impact

- All existing, retained/transplanted trees at the works areas should be properly fenced off and regularly inspected.

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON-SITE.
ALL RIGHTS RESERVED.
© OVE ARUP & PARTNERS HONG KONG LIMITED.

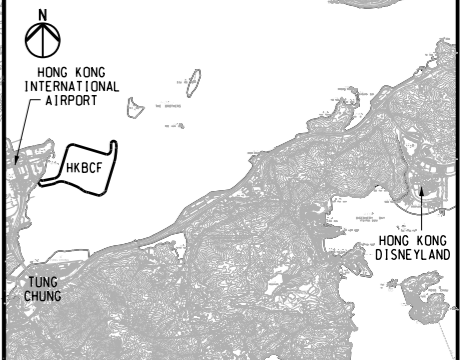

KEY PLAN

- NOTES**
1. ALL COORDINATES ARE RELATED TO HONG KONG 1980 GRID.
 2. ALL LEVELS ARE IN METRES ABOVE HONG KONG PRINCIPAL DATUM (mPD).
 3. REFER TO DRG NO. 211036/SL/1002 FOR THE DEFINITION OF SETTING OUT LINE (SOL) FOR THE HONG KONG BOUNDARY CROSSING FACILITIES (HKBCF) RECLAMATION SITE.
 4. REFER TO DRG NO. 211036/SL/1004 FOR DETAILS OF SITE BOUNDARY.
 5. FOR EXTENT OF SORTING FACILITIES AT FILL BANK AT TSEUNG KWAN O AREA 137 REFER TO DRG NO. 211036/SL/1015.

- LEGEND**
- - - - - SITE BOUNDARY
 - - - - - SETTING OUT LINE (SOL)
 - - - - - WORKS AREA BOUNDARY

Rev	Description	By	Date
-	FOR CONSTRUCTION	HYJL	11/11

Consultant

ARUP 奧雅納工程顧問 •
Ove Arup & Partners Hong Kong Limited

Supported By :

- Ecosystems Ltd. ○
- EDA Marine Ltd. ○
- Geotechnical Consulting Group (Asia) Ltd. ○
- Hong Kong Cetacean Research Project ○
- IntelBuild Technyx Asia Limited ○
- Tony Gee and Partners LLP ○

Contract No. and Title:
Contract No. HY/2010/02
Hong Kong-Zhuhai-Macao Bridge
Hong Kong Boundary Crossing Facilities
- Reclamation Works


Drawing title
KEY PLAN

Drawing no. 211036/SL/1001		Rev. -	
Drawn RL	Date 11/09	Checked KKY	Approved DML
Scale 1:20000 @A1 1:40000 @A3		Status WORKING	


COPYRIGHT RESERVED

路政署 HIGHWAYS DEPARTMENT
港珠澳大橋香港工程管理局
Hong Kong - Zhuhai - Macao Bridge
Hong Kong Project Management Office

Printed by : 12/17/2011
Filename : J:\211036\RECORD\WORKING\20111130_Contract Drawing_211036_SL_1001.dgn

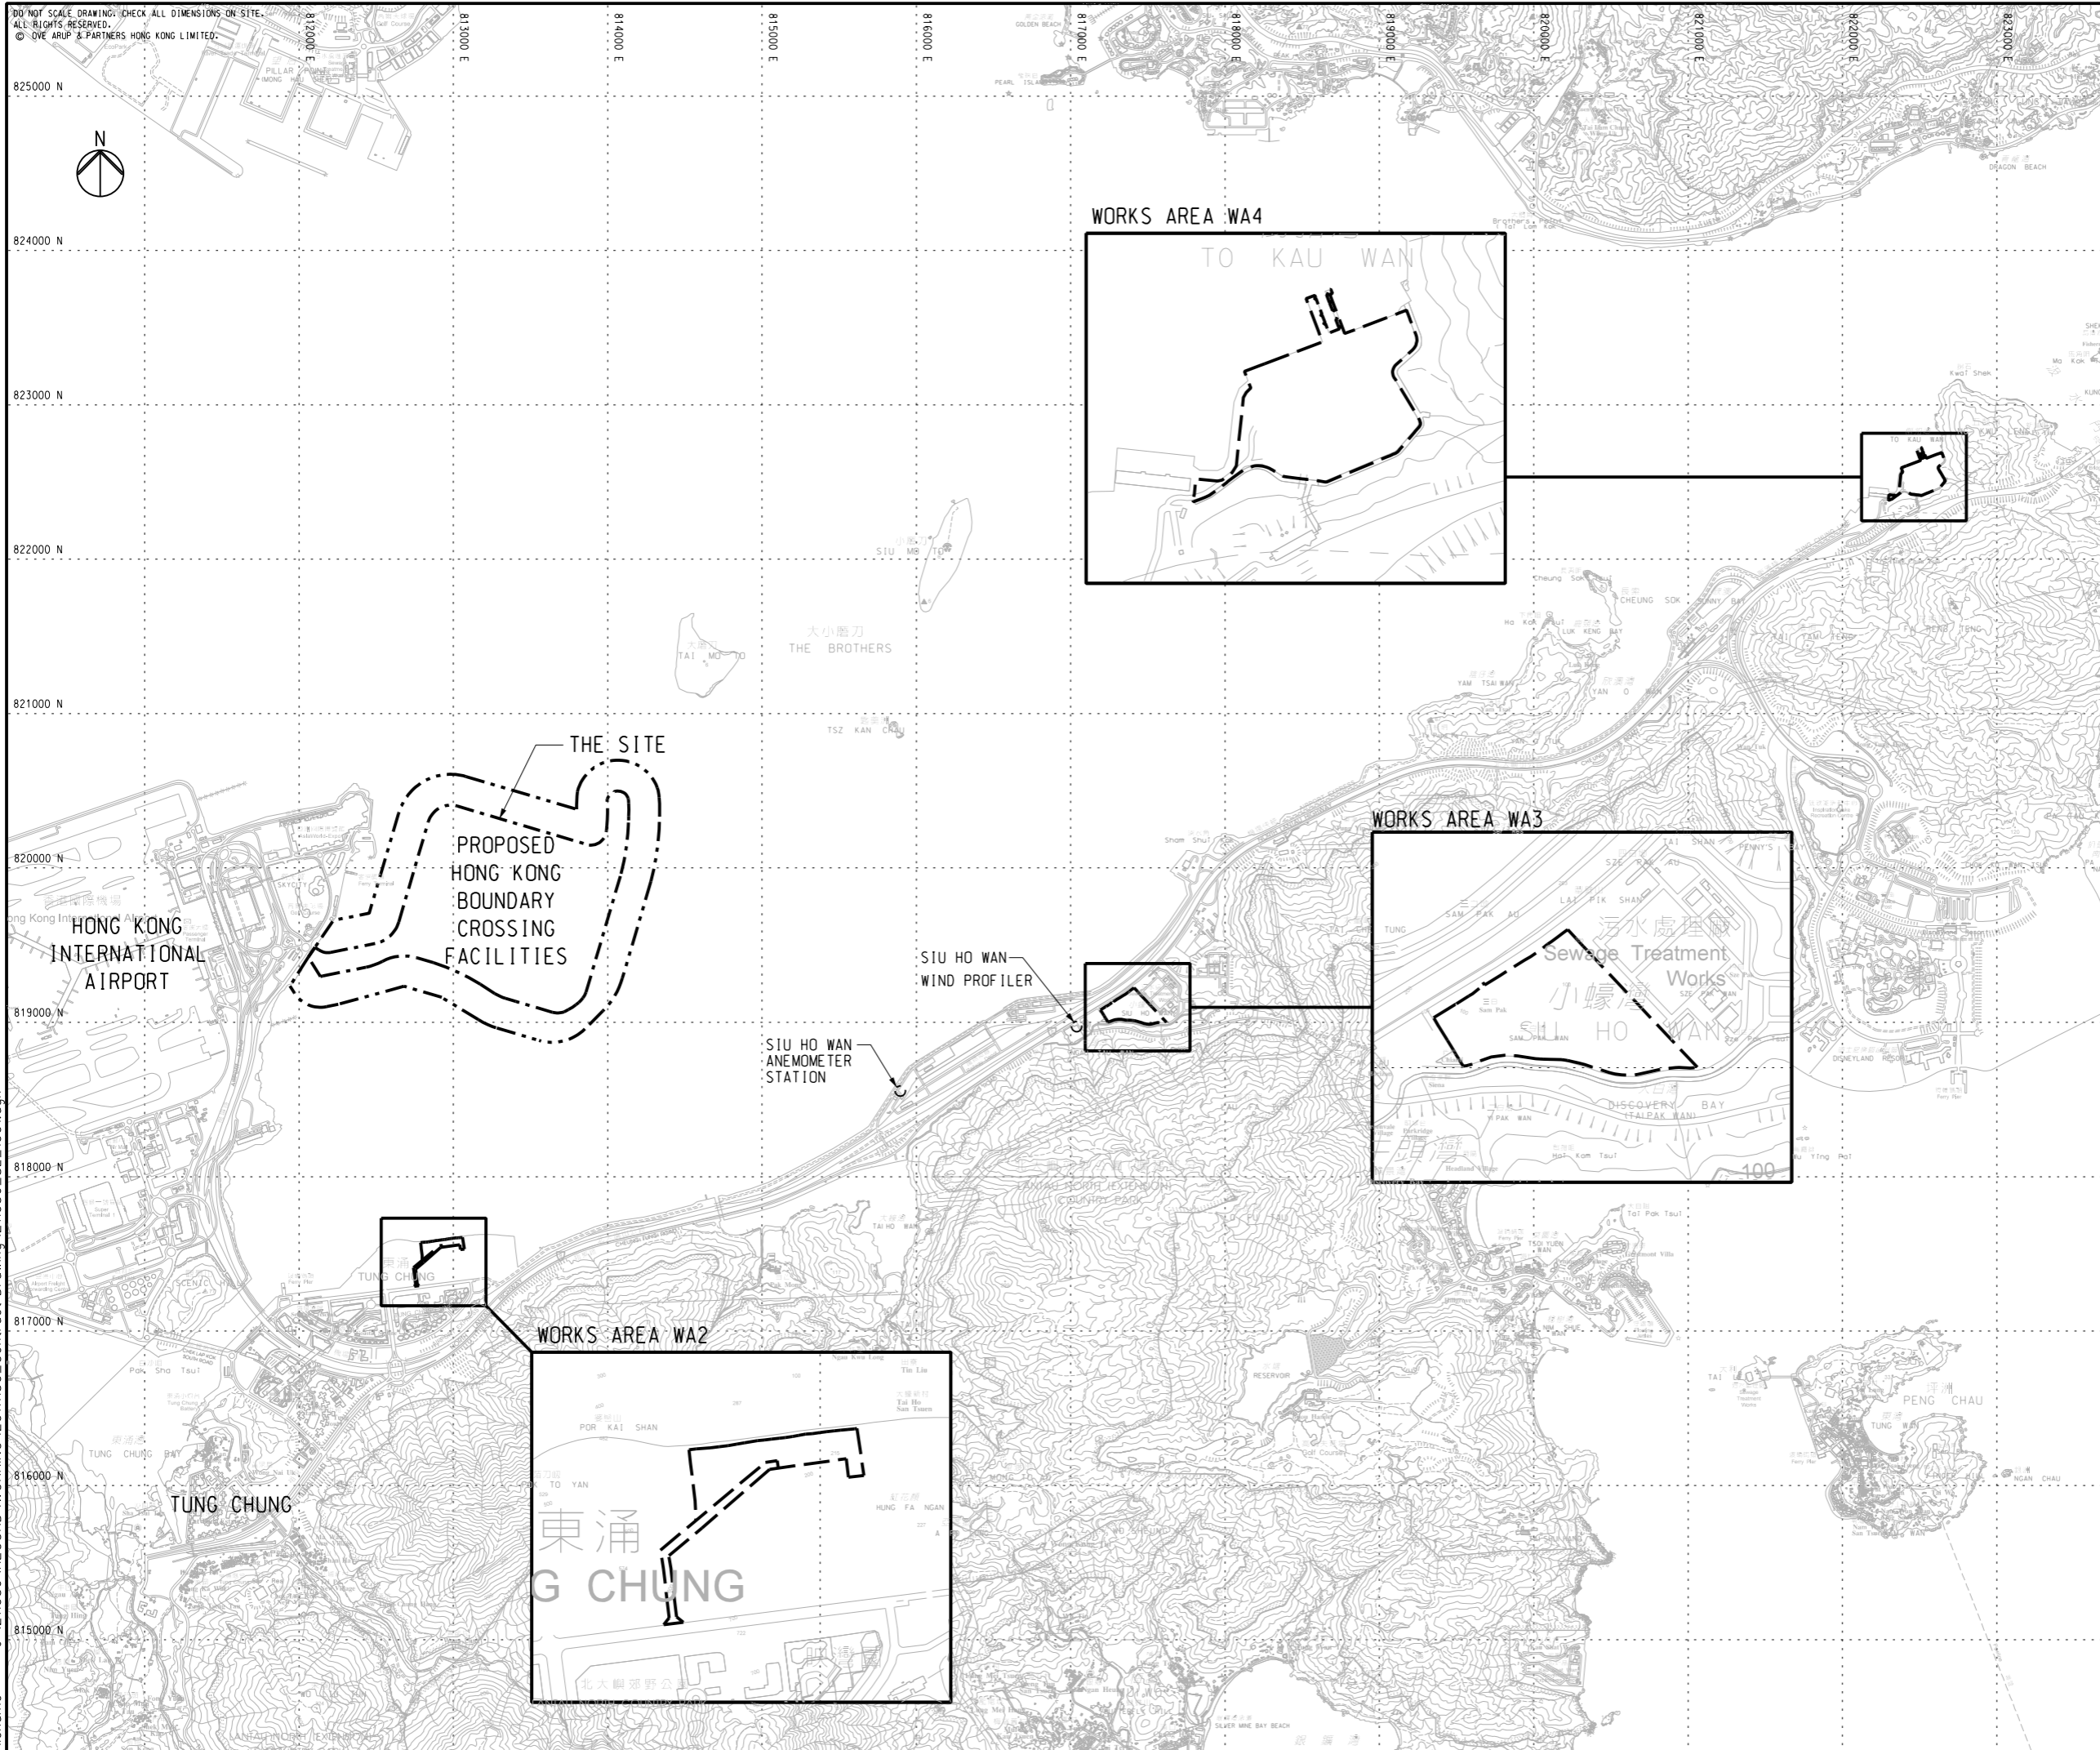

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© OVE ARUP & PARTNERS HONG KONG LIMITED.

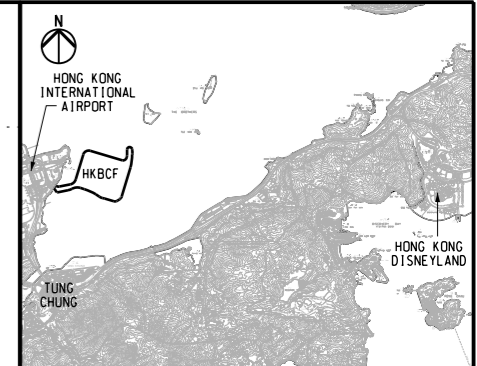

KEY PLAN

NOTES

- FOR LEGENDS AND NOTES FOR CHAIN LINK FENCE AND GATE REFER TO DRG NO. 211036/SL/1013.
- THE ERECTION OF CHAIN LINK FENCE AND GATES SHALL BE COMPLETED BY THE HANDOVER DATE OF EACH PORTION OF SITE, OR AS INSTRUCTED BY THE ENGINEER.
- FOR SETTING OUT COORDINATES OF DIFFERENT PORTIONS OF SITE REFER TO DRG NO. 211036/SL/1003.
- ACCESS POINTS BETWEEN PORTIONS SHALL BE PROVIDED BY THE CONTRACTOR, AND THE LOCATIONS SHALL BE AGREED WITH THE ENGINEER ON SITE.
- FOR HOARDING AND FENCE AT FILL BANK AT TSEUNG KWAN O AREA 137 REFER TO DRG NO. 211036/SL/1015.

LEGEND

- SETTING OUT LINE (SOL)
- WORKS AREA BOUNDARY
- PORTIONS BOUNDARY LINE

Rev	Description	By	Date
-	FOR CONSTRUCTION	HYJL	11/11

Consultant

ARUP	奧雅納工程顧問	●
Ove Arup & Partners Hong Kong Limited		
Supported By :	Ecosystems Ltd.	○
	EDA Marine Ltd.	○
	Geotechnical Consulting Group (Asia) Ltd.	○
	Hong Kong Cetacean Research Project	○
	Intel:Build Technyx Asia Limited	○
	Tony Gee and Partners LLP	○

Contract No. and Title:
Contract No. HY/2010/02
Hong Kong-Zhuhai-Macao Bridge
Hong Kong Boundary Crossing Facilities
- Reclamation Works


Drawing title
WORKS AREA LAYOUT
AND HOARDING PLAN
(SHEET 2 OF 3)



Drawing no. 211036/SL/1014		Rev. -	
Drawn RL	Date 06/10	Checked KKY	Approved DML
Scale 1:5000 @A1 1:10000 @A3		Status WORKING	

COPYRIGHT RESERVED

路政署
HIGHWAYS DEPARTMENT
 港珠澳大橋香港工程管理局
 Hong Kong - Zhuhai - Macao Bridge
 Hong Kong Project Management Office

Printed by : 12/17/2011
 Filename : J:\211036\RECORD\WORKING\20111130_Contract Drawing_211036_SL_1014.dgn

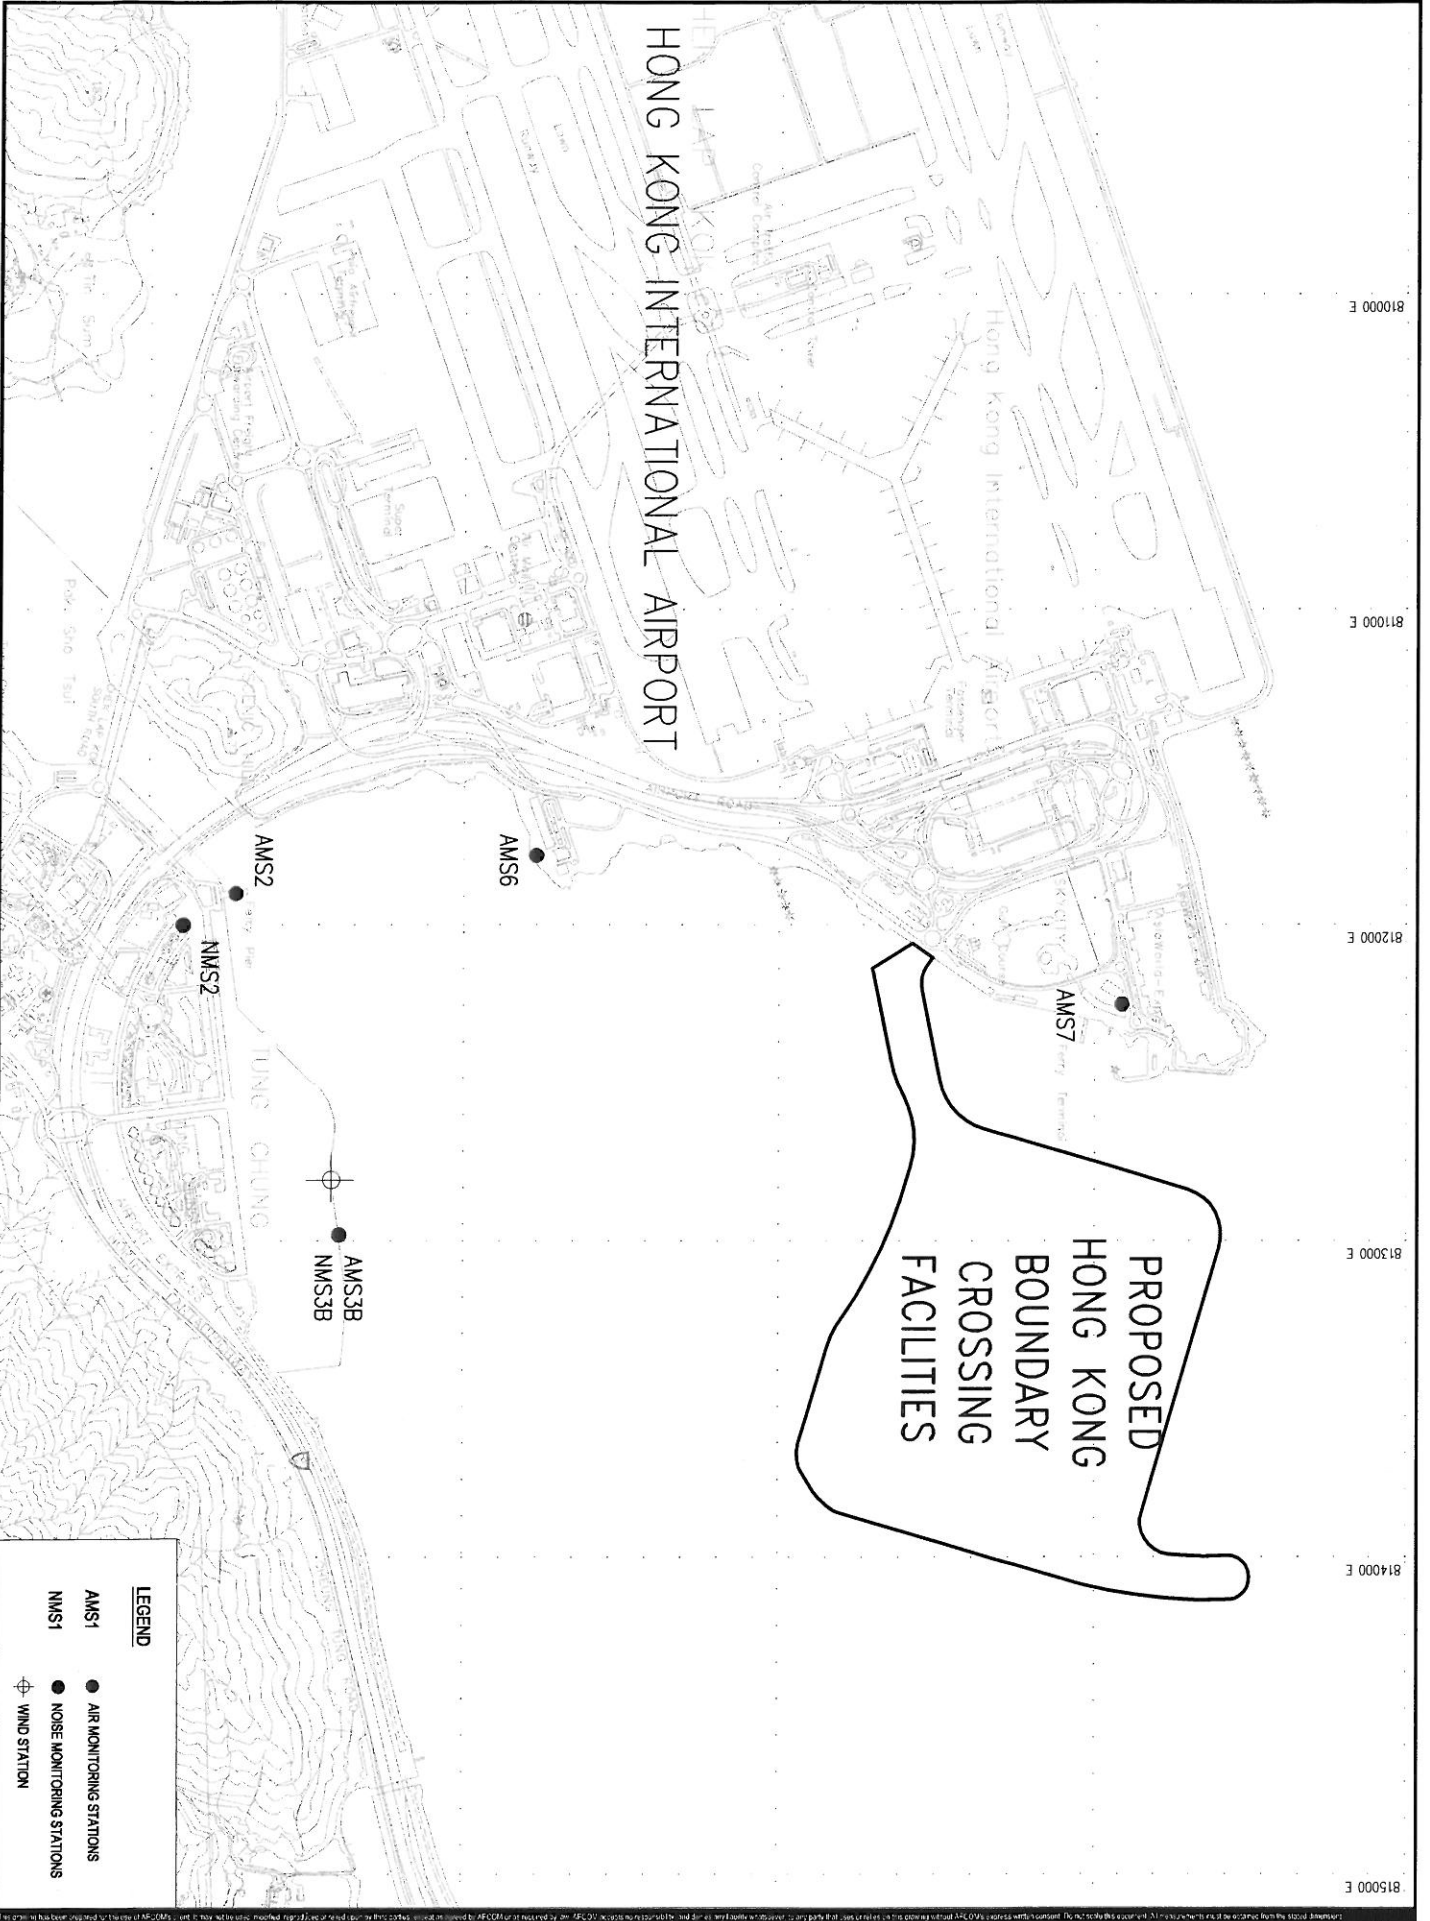


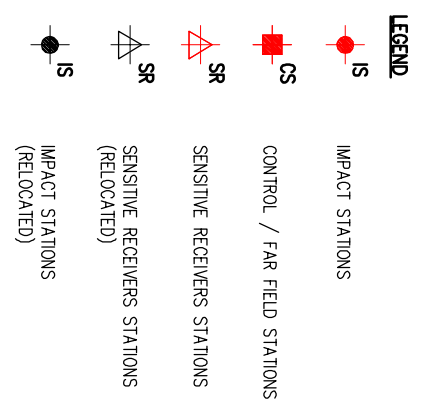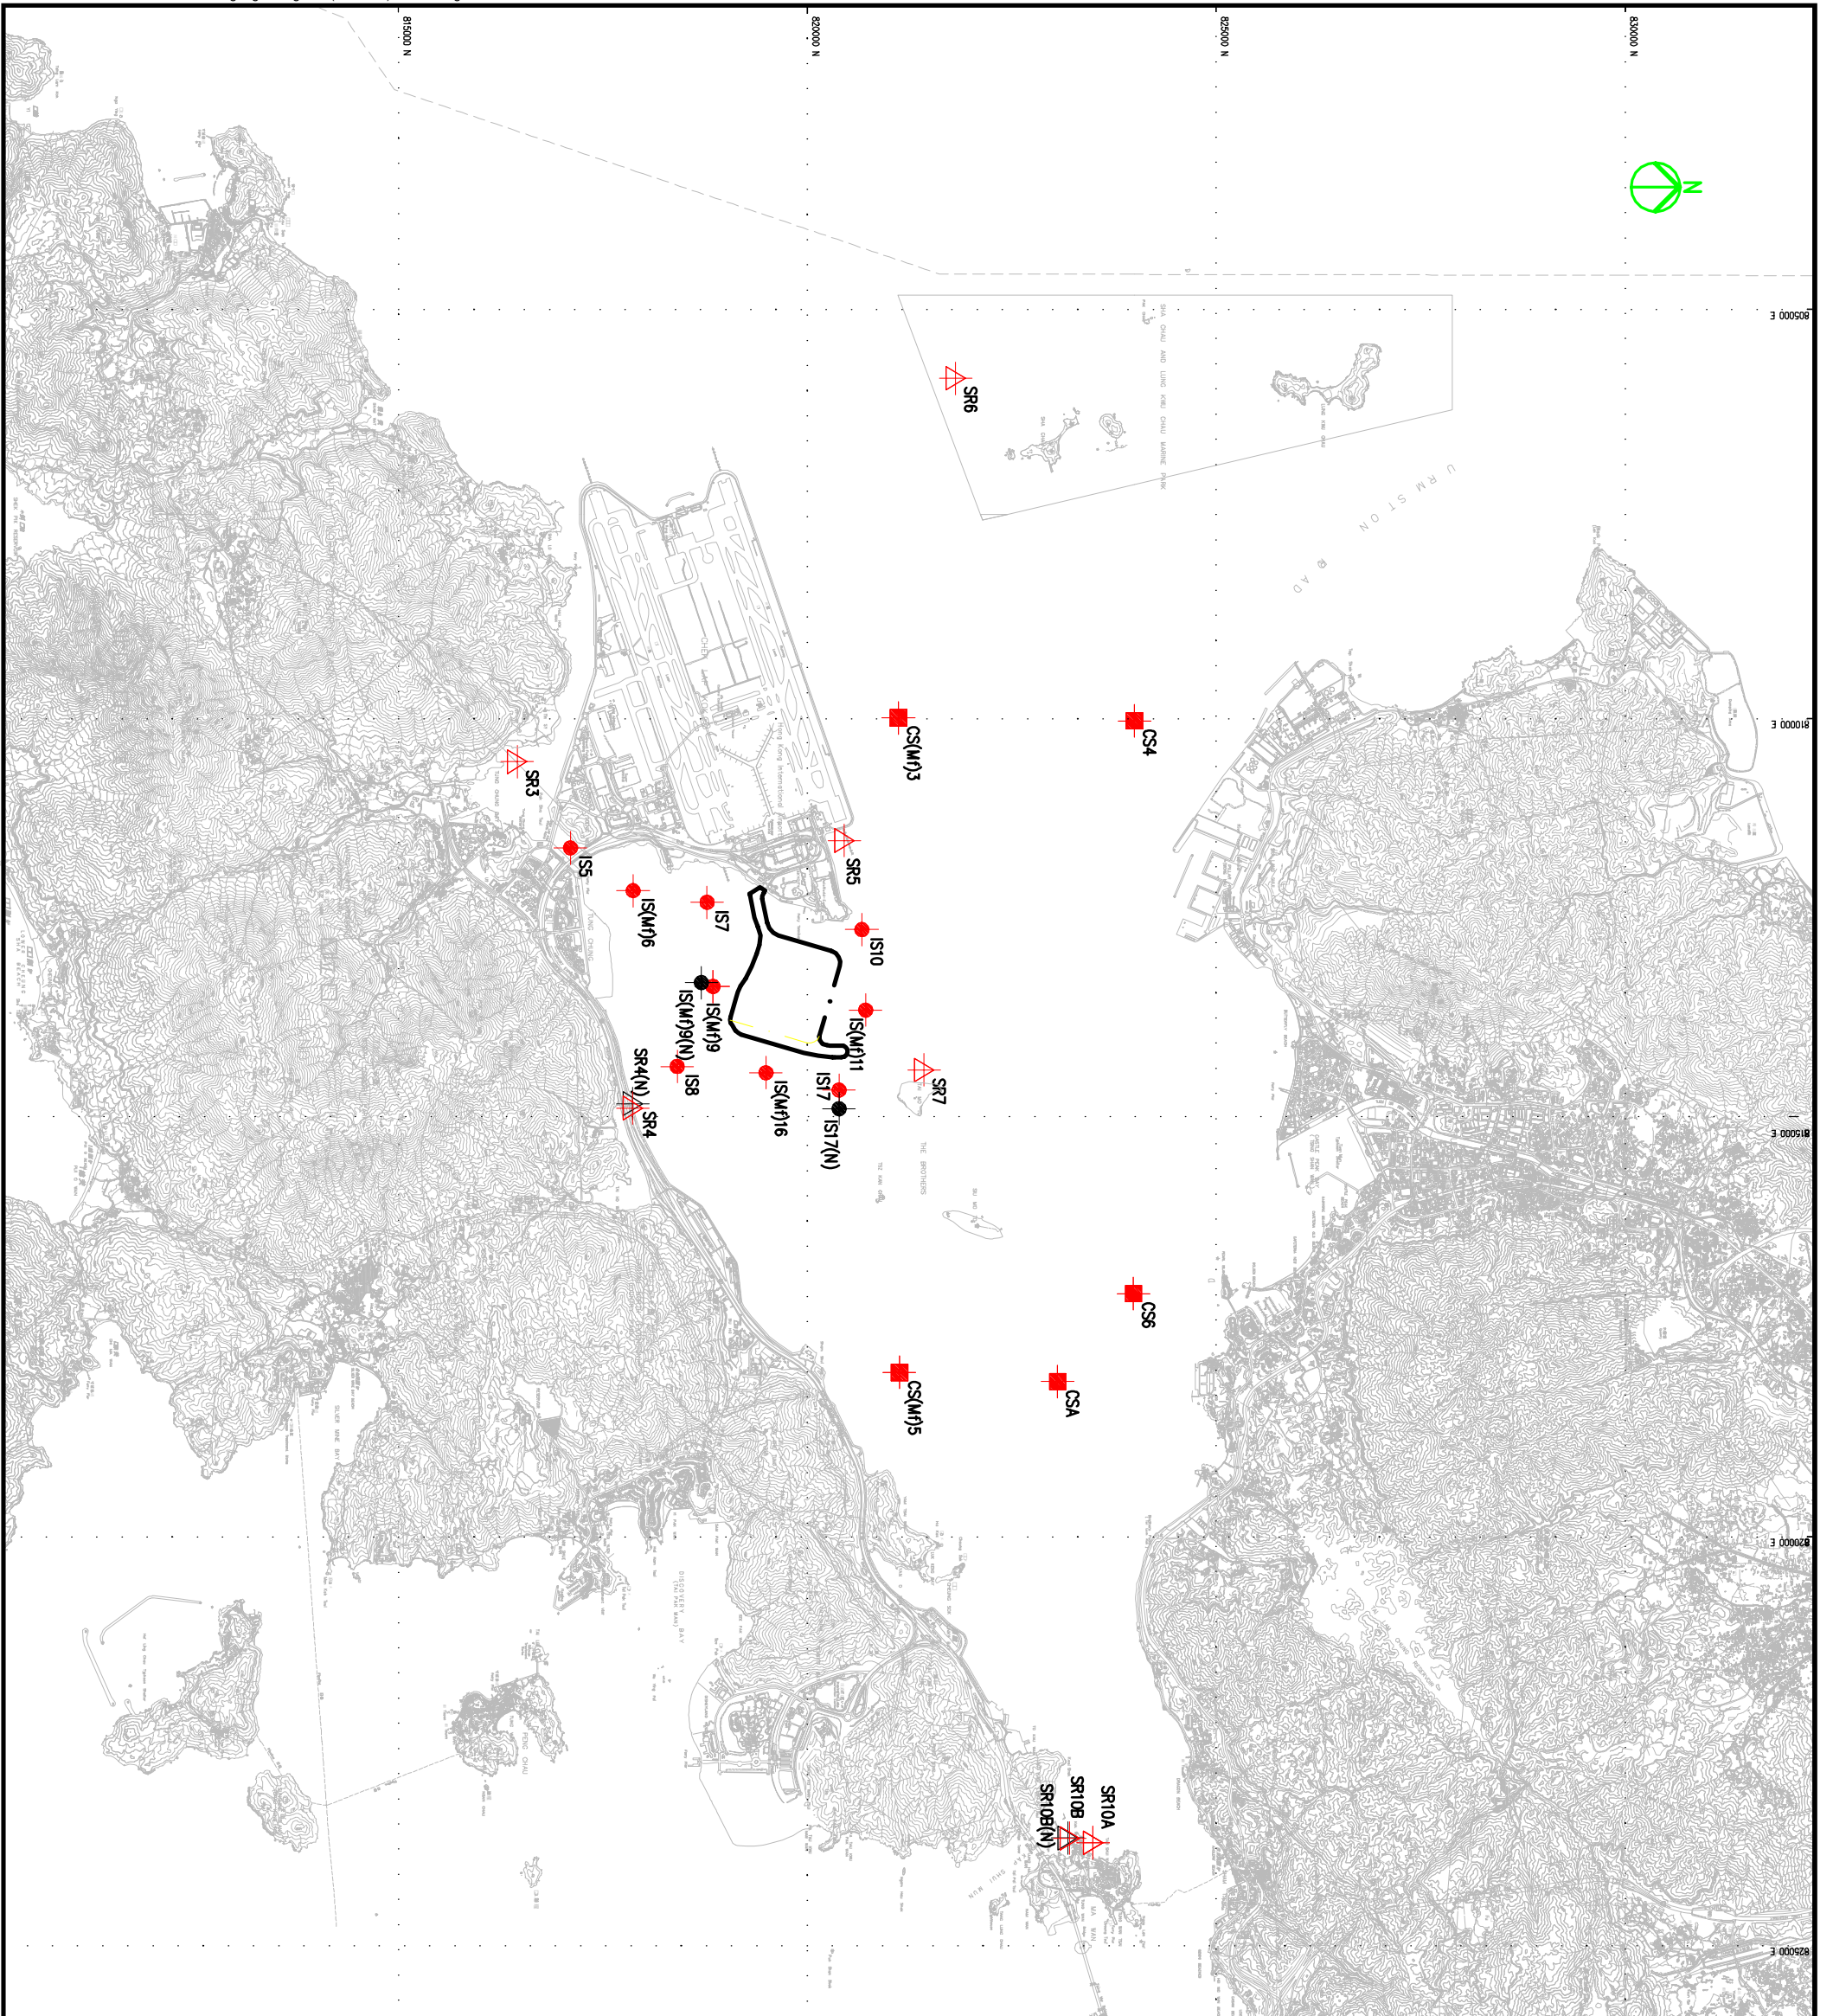

SETTING OUT SCHEDULE

MONITORING STATIONS	CO-ORDINATES	
	EASTING	NORTHING
IS5	811579	817106
IS(M)16	812101	817873
IS7	812244	818777
IS8	814251	818412
IS(M)9	813273	818850
IS(M)9(N)	813226	818708
IS10	812577	820670
IS(M)11	813562	820716
IS(M)16	814328	819497
IS17	814539	820391
IS17(N)	814767	820391
SR3	810525	816456
SR4(N)	814705	817859
SR5	811489	820455
SR6	805837	821818
SR7	814293	821431
SR10A	823741	823495
SR10B(N)	823683	823187
CS(M)3	809989	821117
CS(M)5	817990	821129
CS4	810025	824004
CS6	817028	823992
CSA	818103	823064

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and disclaims any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

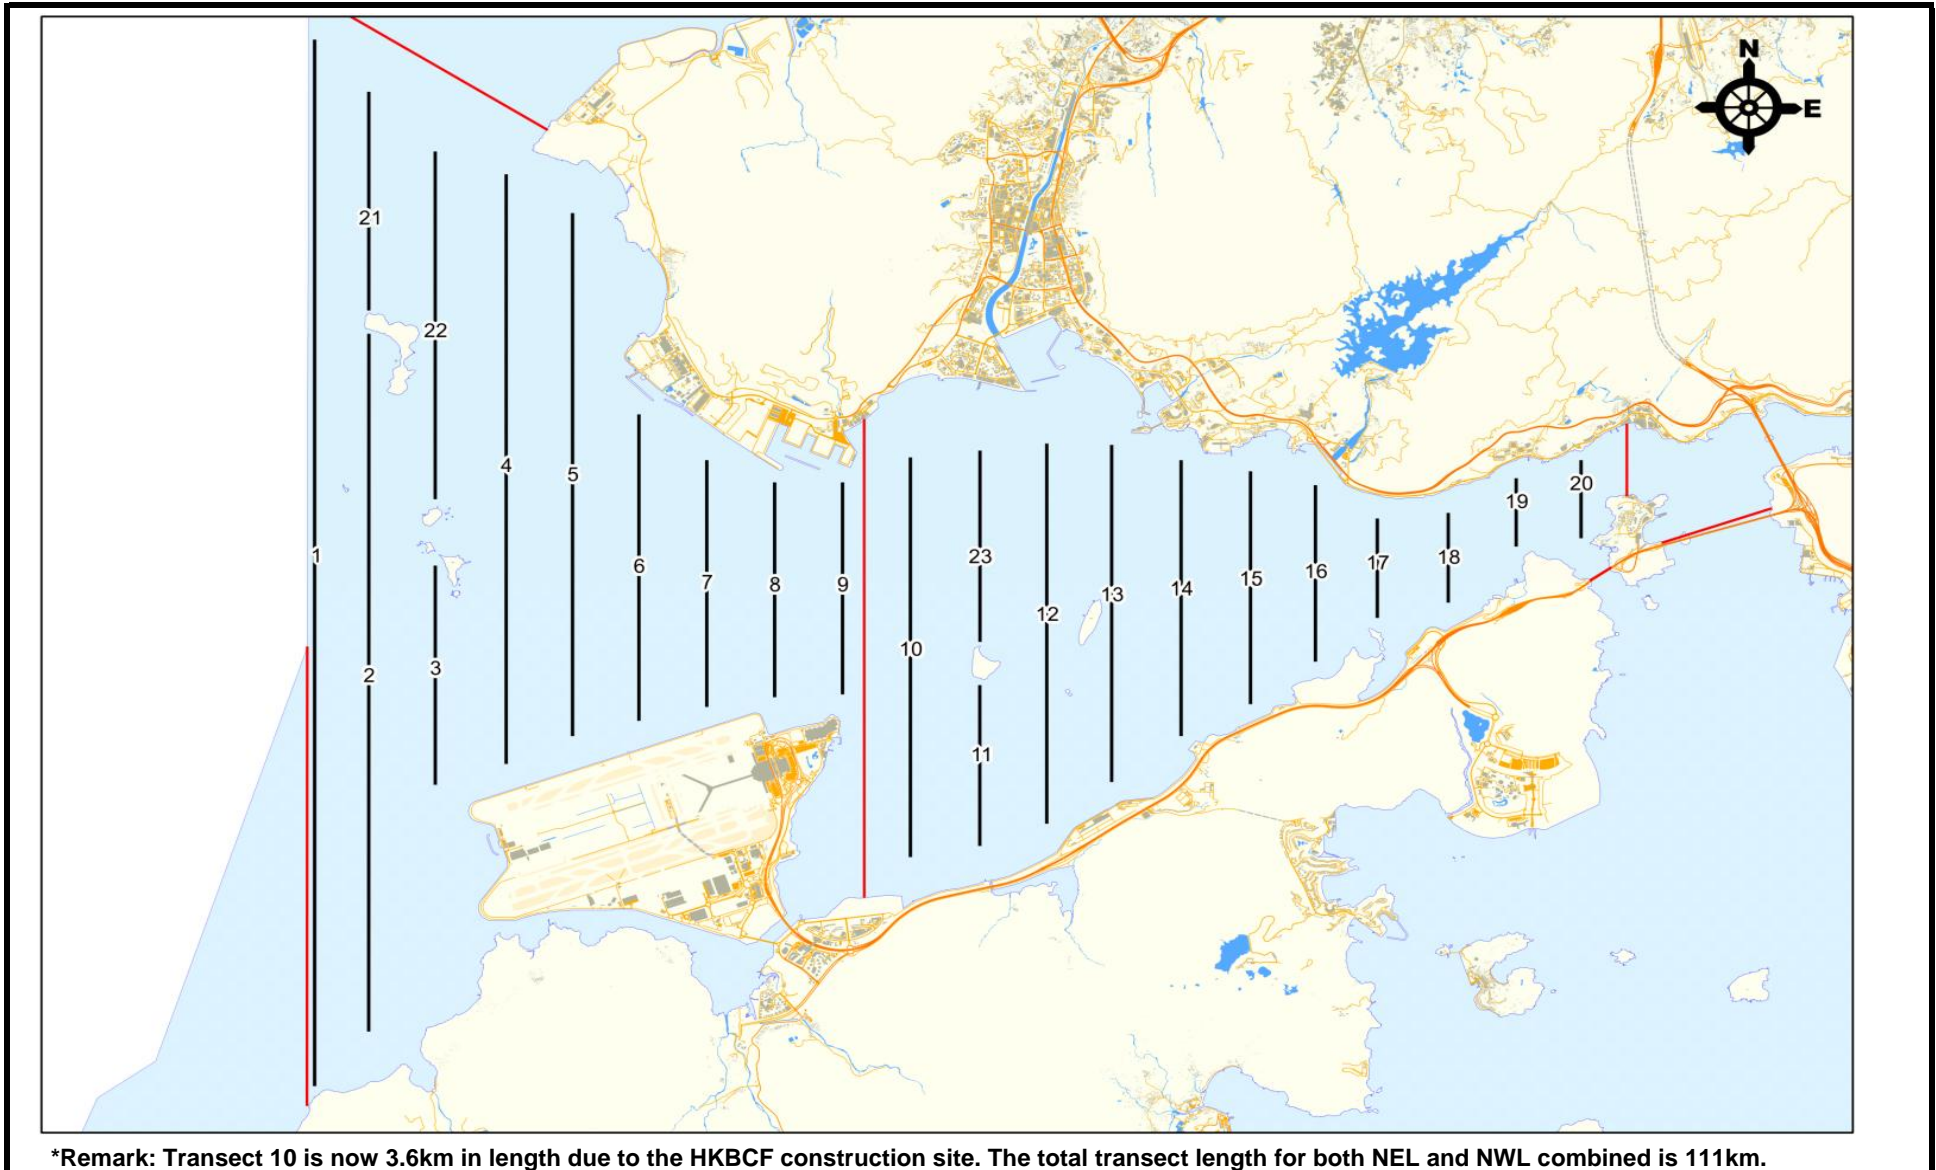


**HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS**
 Project No.: 60249820 Date: January 13

**Impact Dolphin Monitoring
 Line Transect Layout Map**



Figure 4

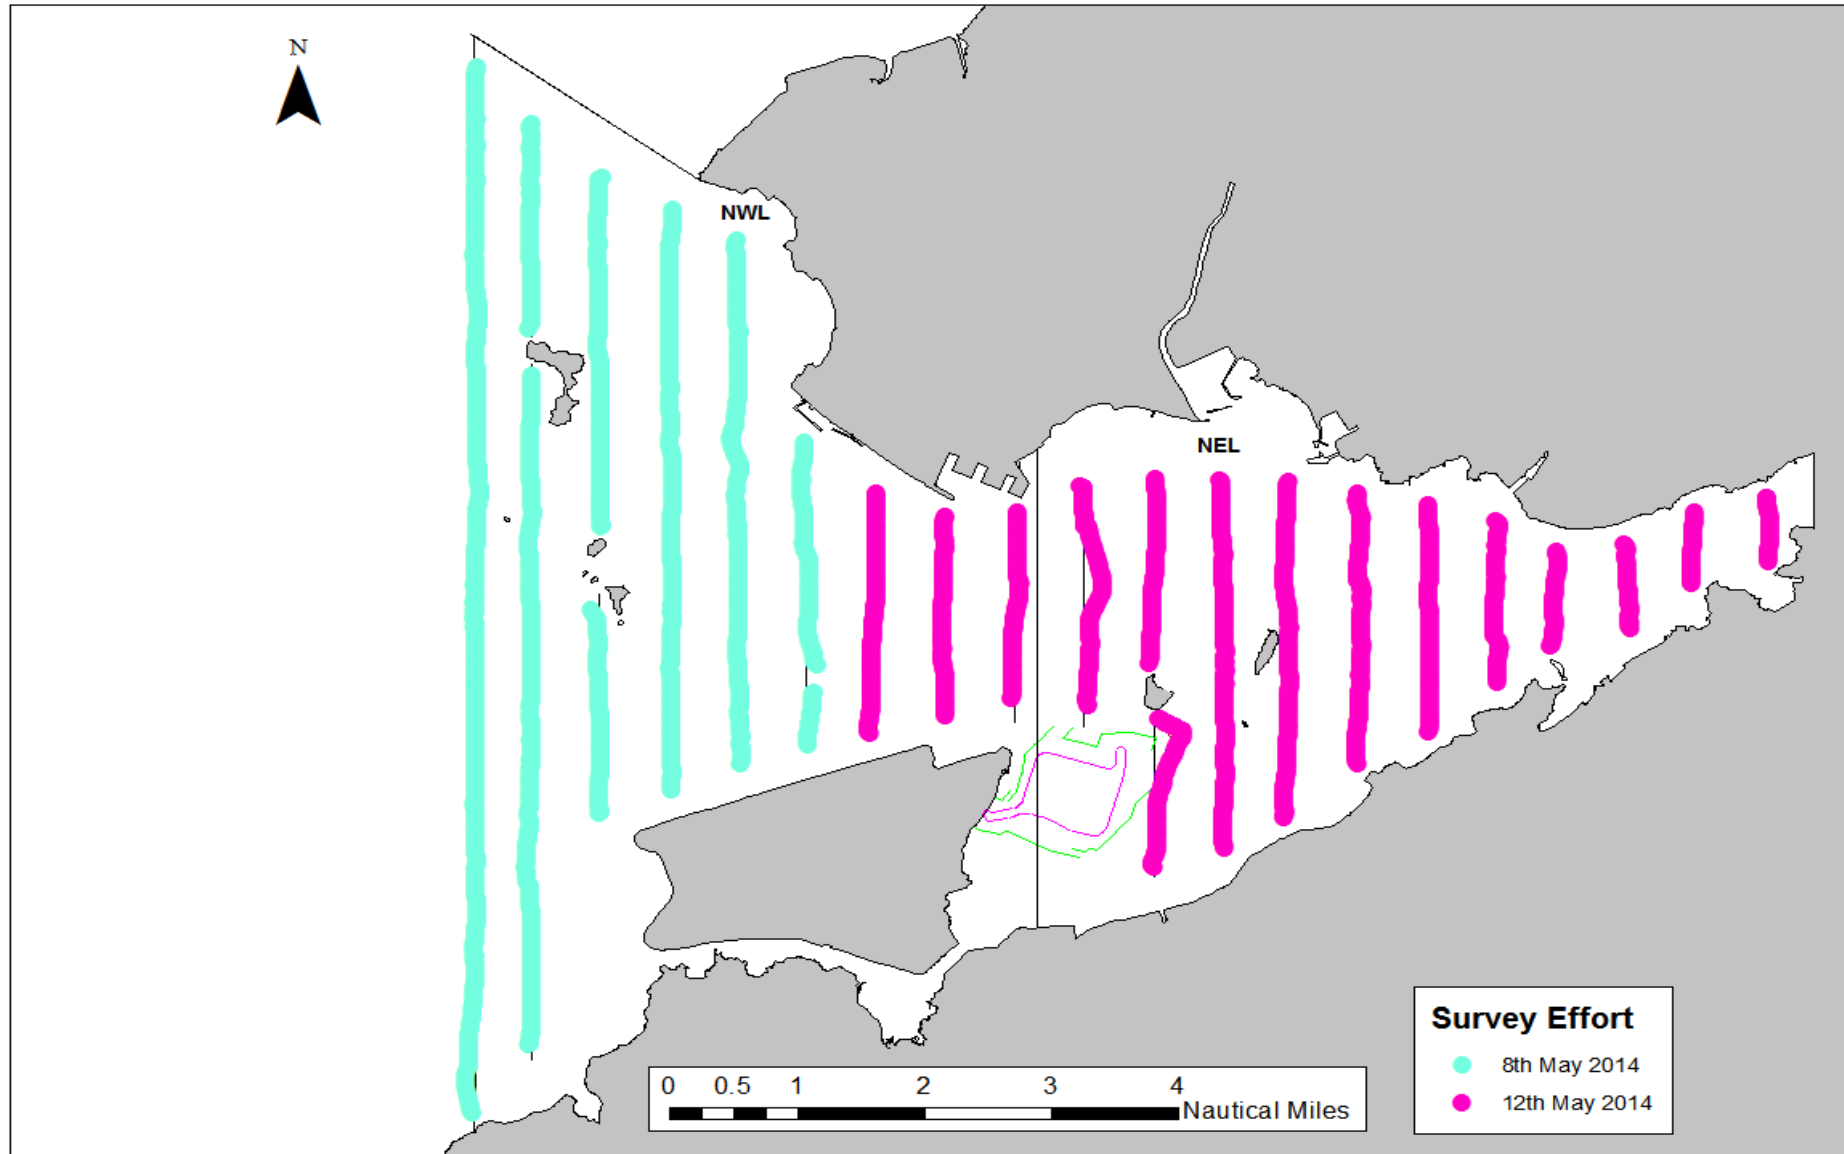


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS
 Project No.: 60249820 Date: June 2014

Impact Dolphin Monitoring Survey Efforts
on 8 and 12 May 2014

Figure 5a

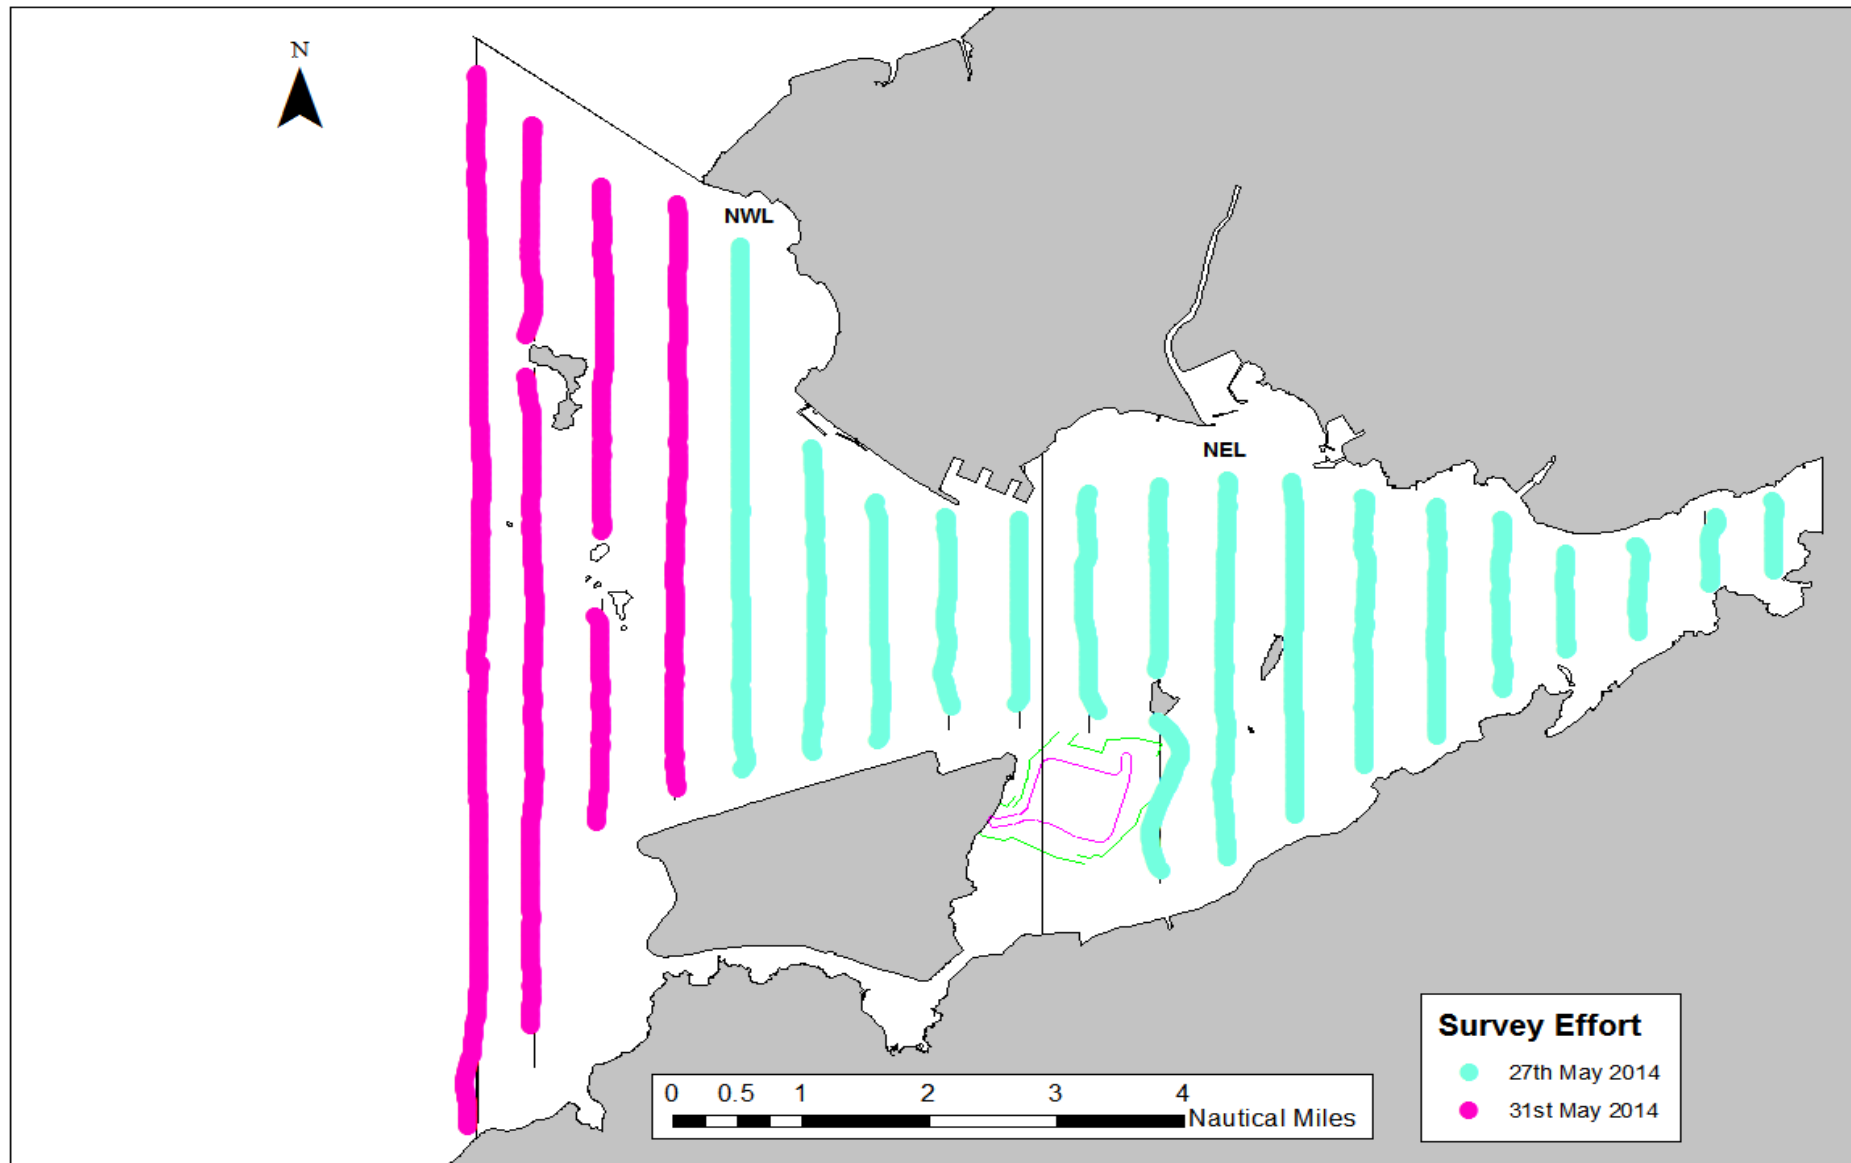


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS
 Project No.: 60249820 Date: June 2014

Impact Dolphin Monitoring Survey Efforts
on 27 and 31 May 2014

Figure 5b

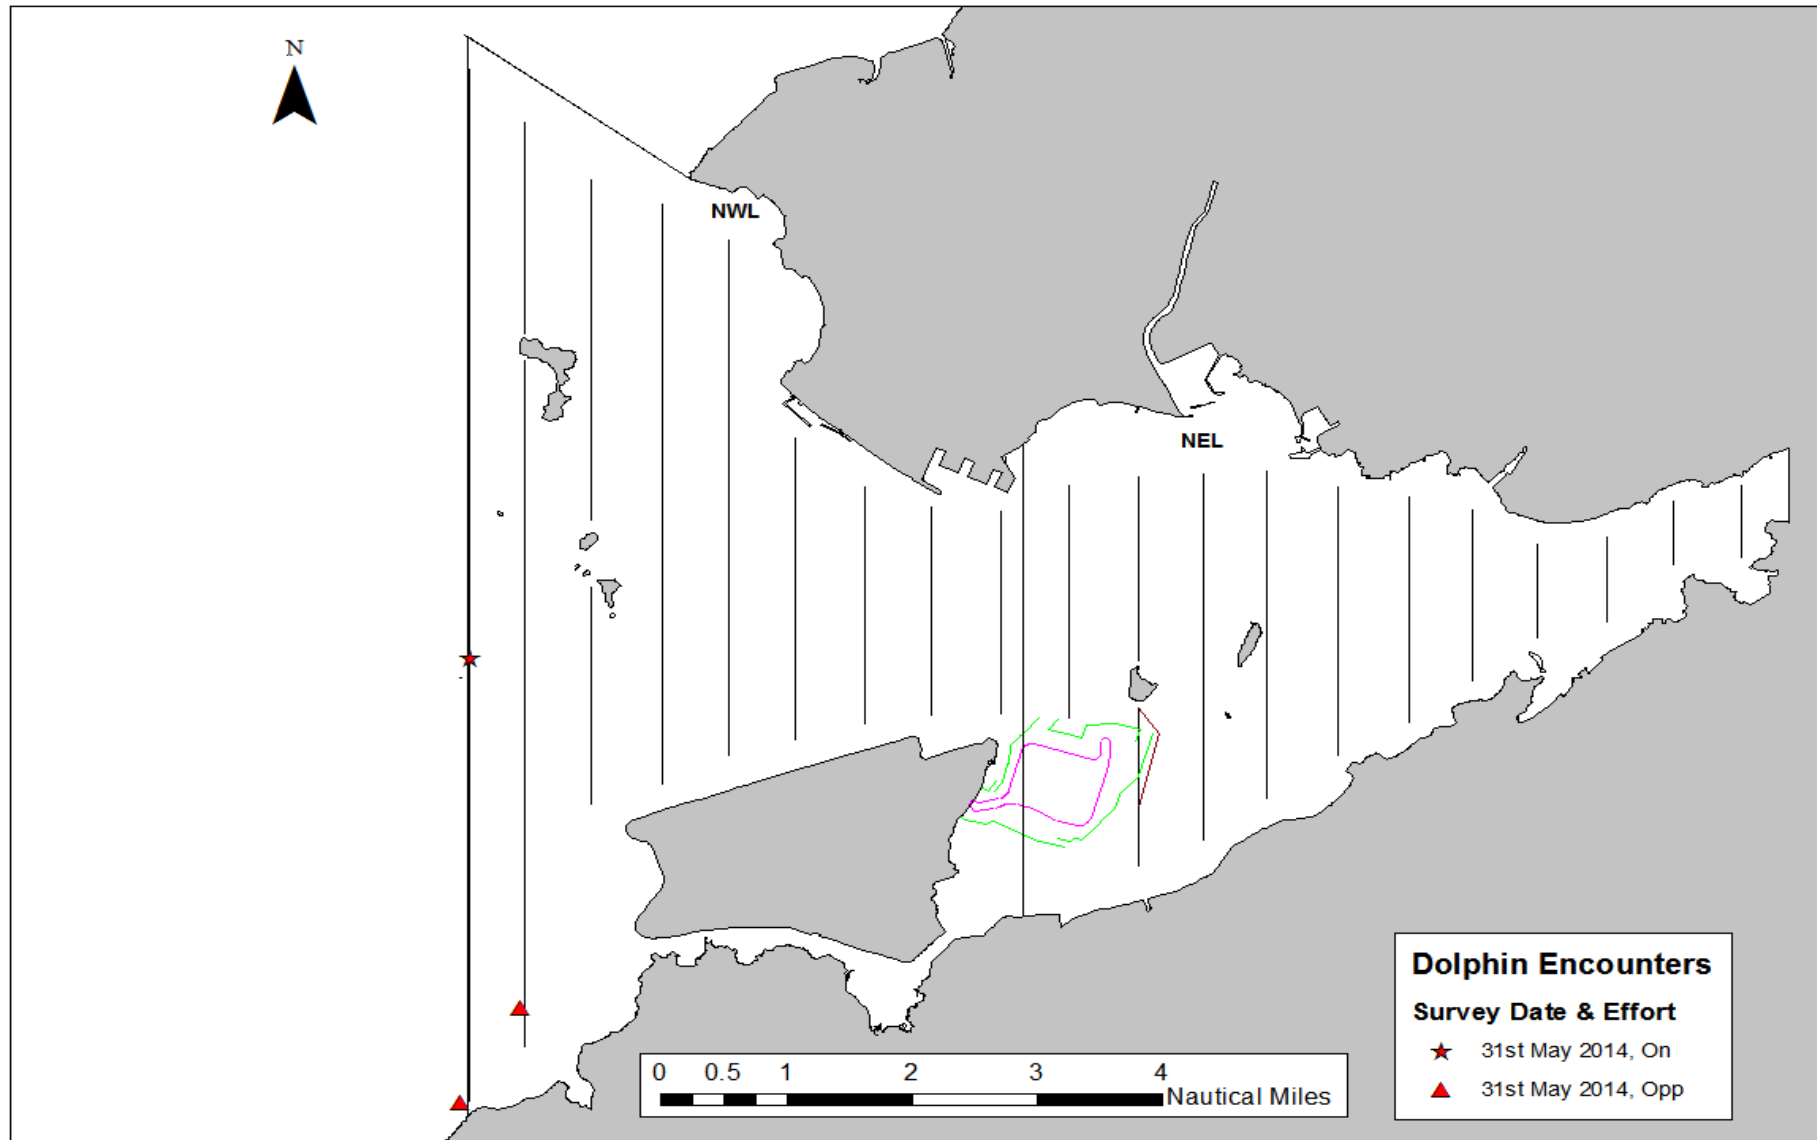


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS
 Project No.: 60249820 Date: June 2014

Impact Dolphin Monitoring Survey
Sightings in May 2014

Figure 5c

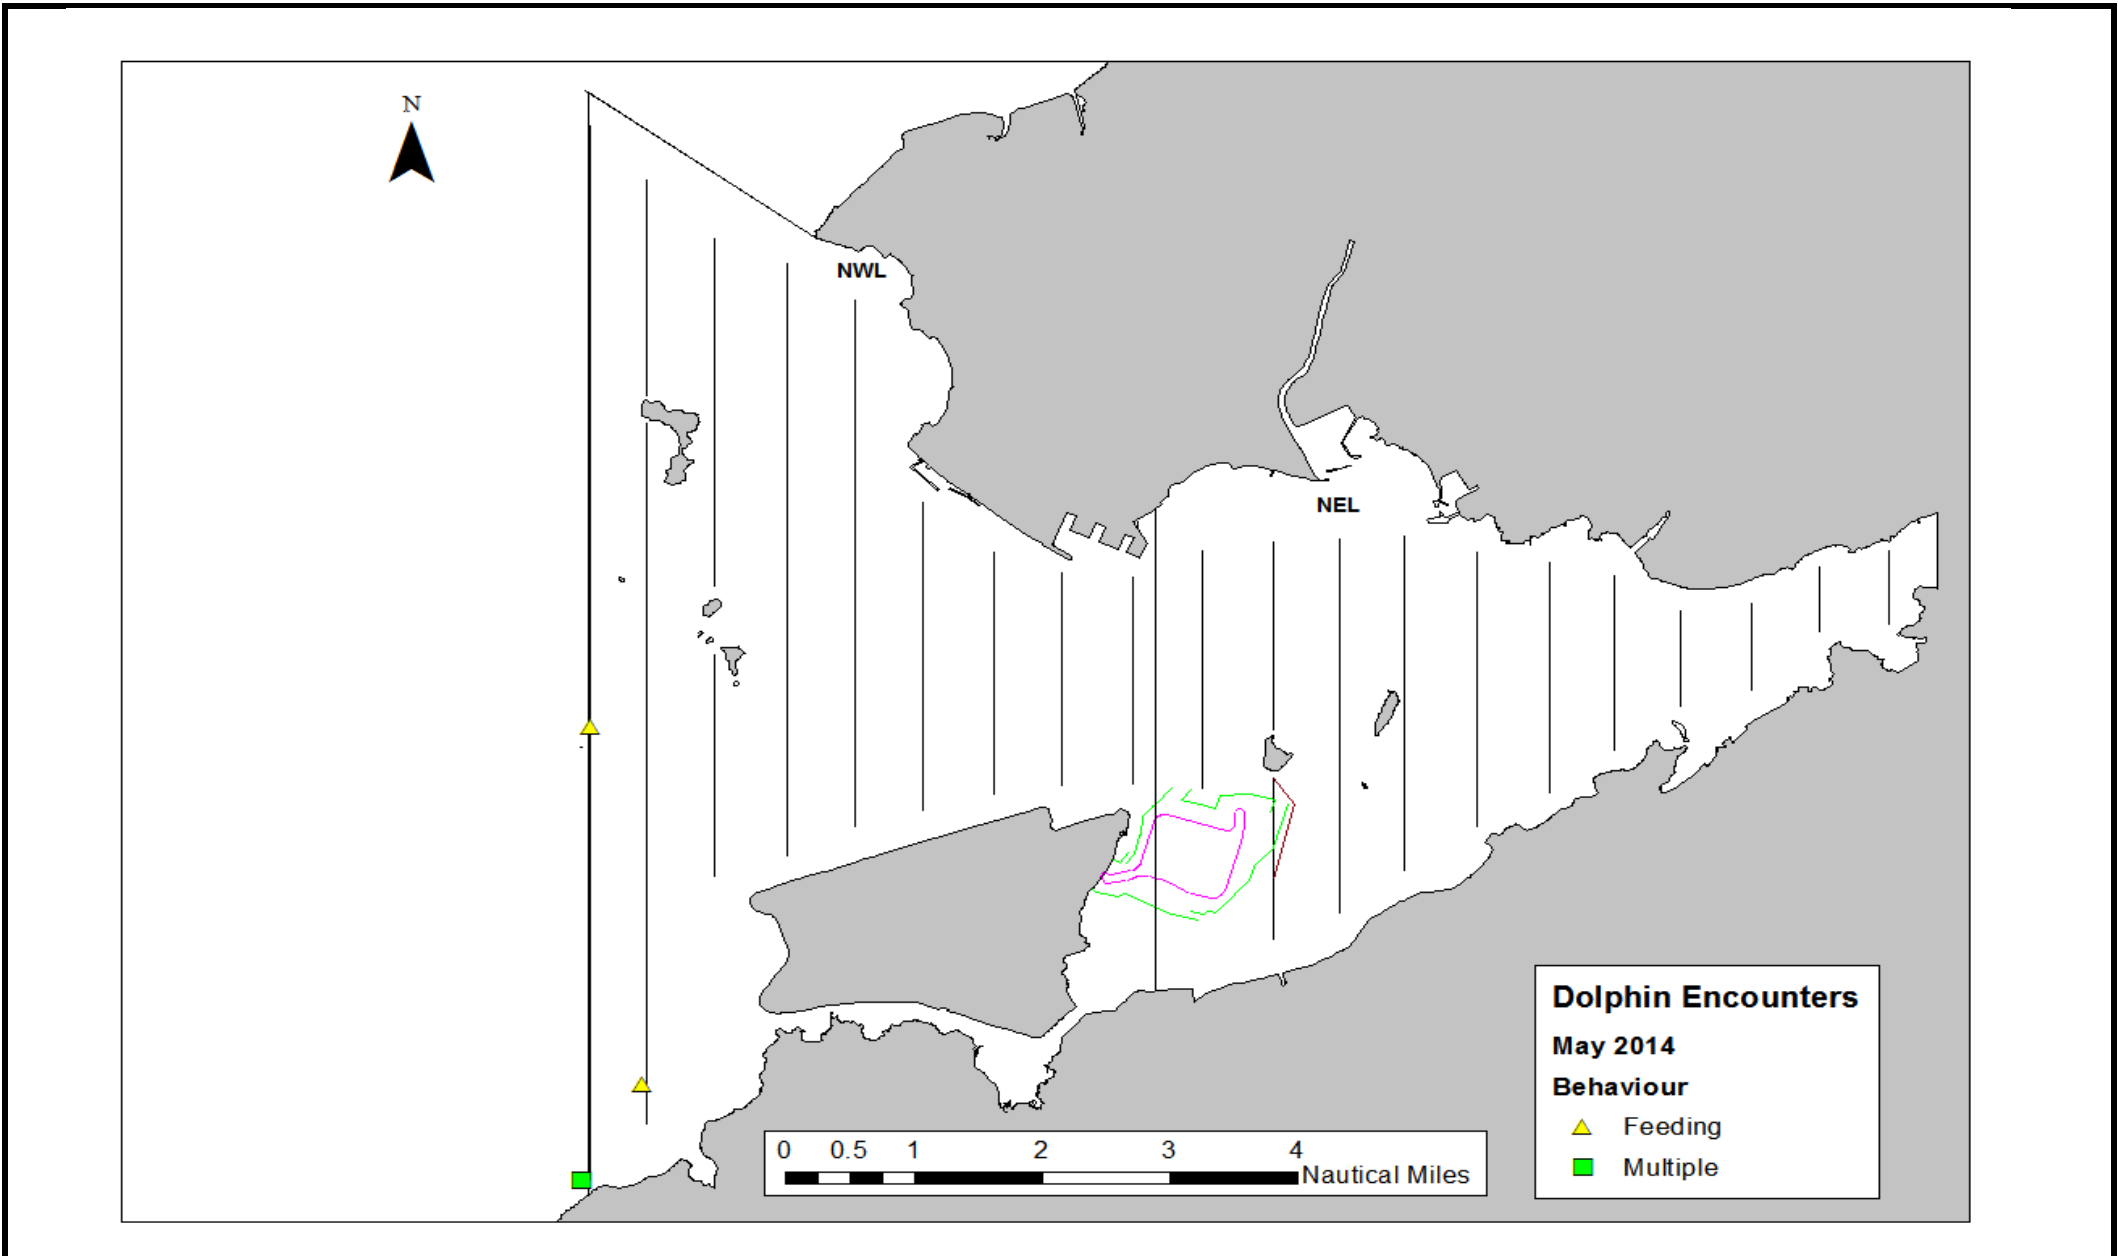


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS
 Project No.: 60249820 Date: June 2014

Impact Dolphin Monitoring Survey
Behaviour Map in May 2014

Figure 5d

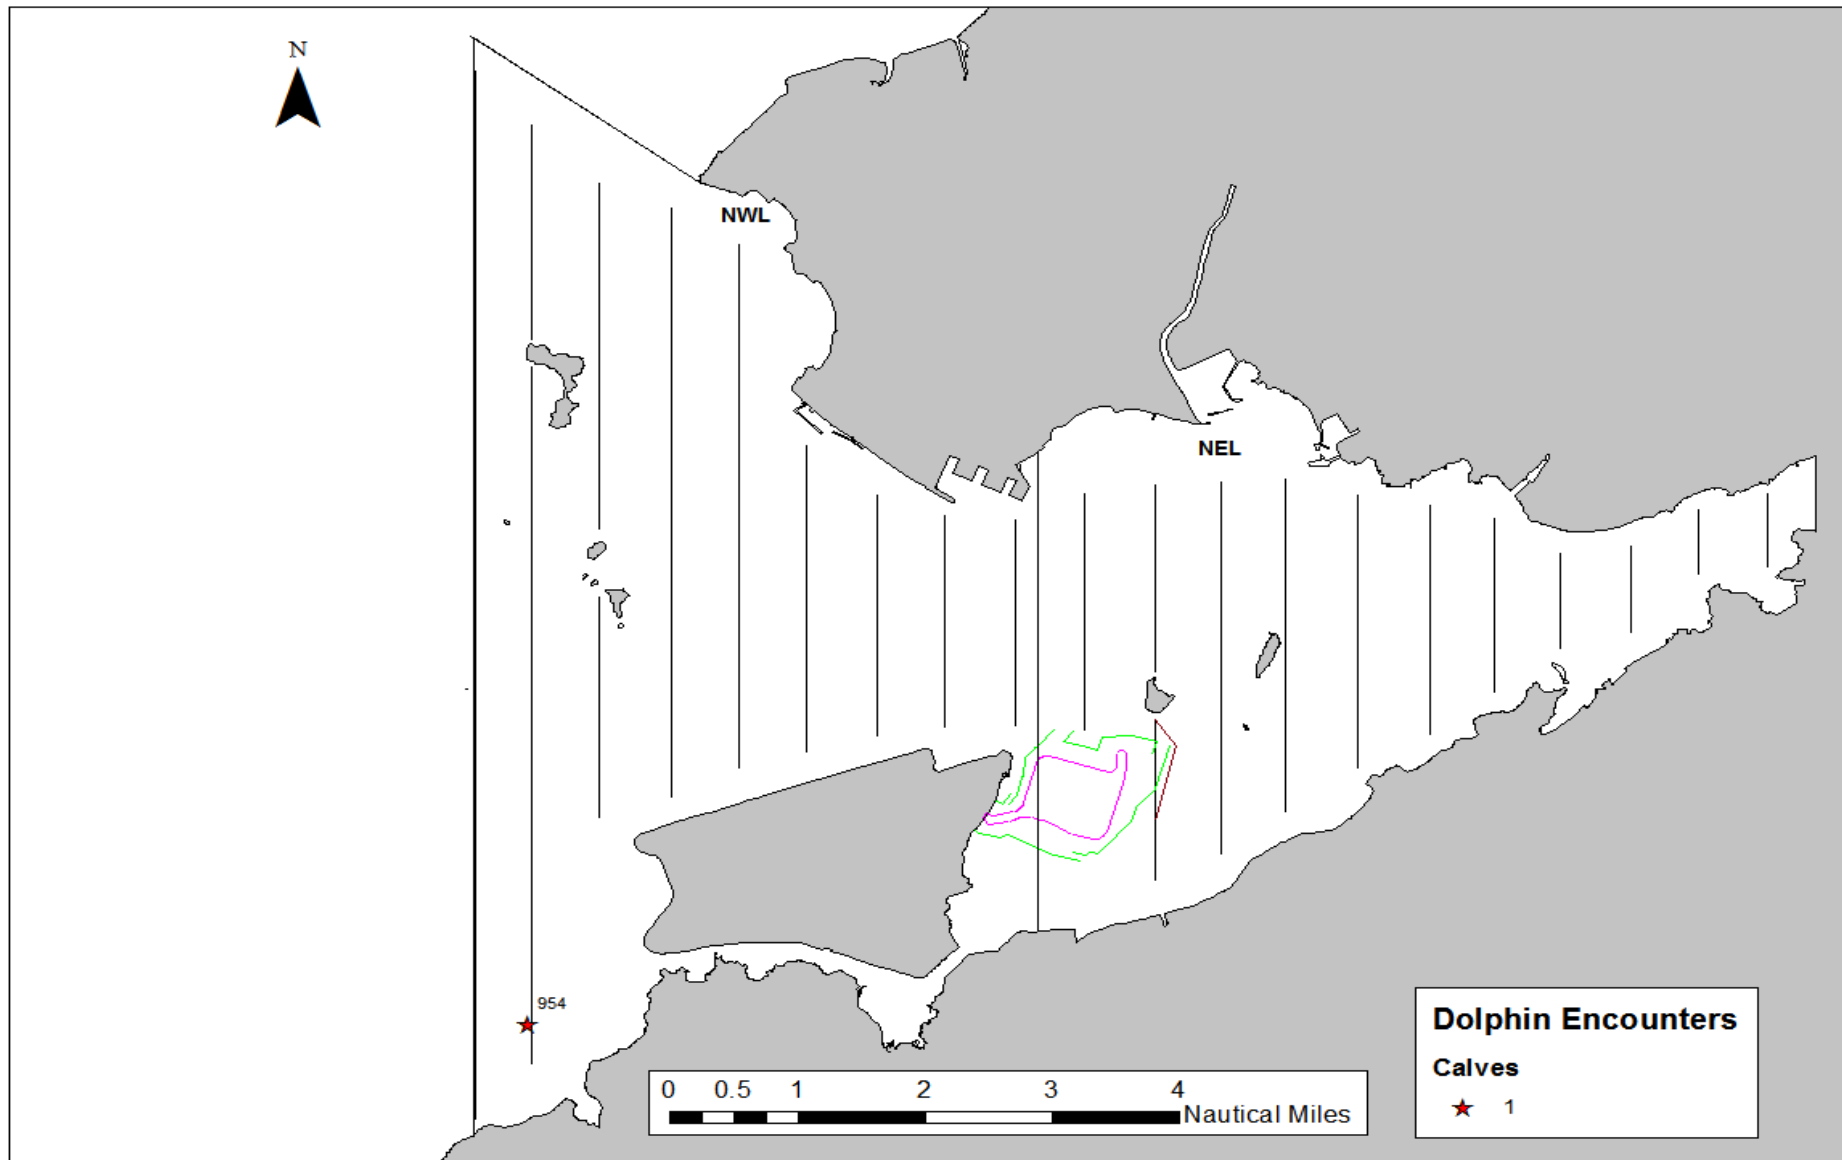


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.


HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS
 Project No.: 60249820 Date: June 2014

Impact Dolphin Monitoring Survey Calf
Map in May 2014

Figure 5e

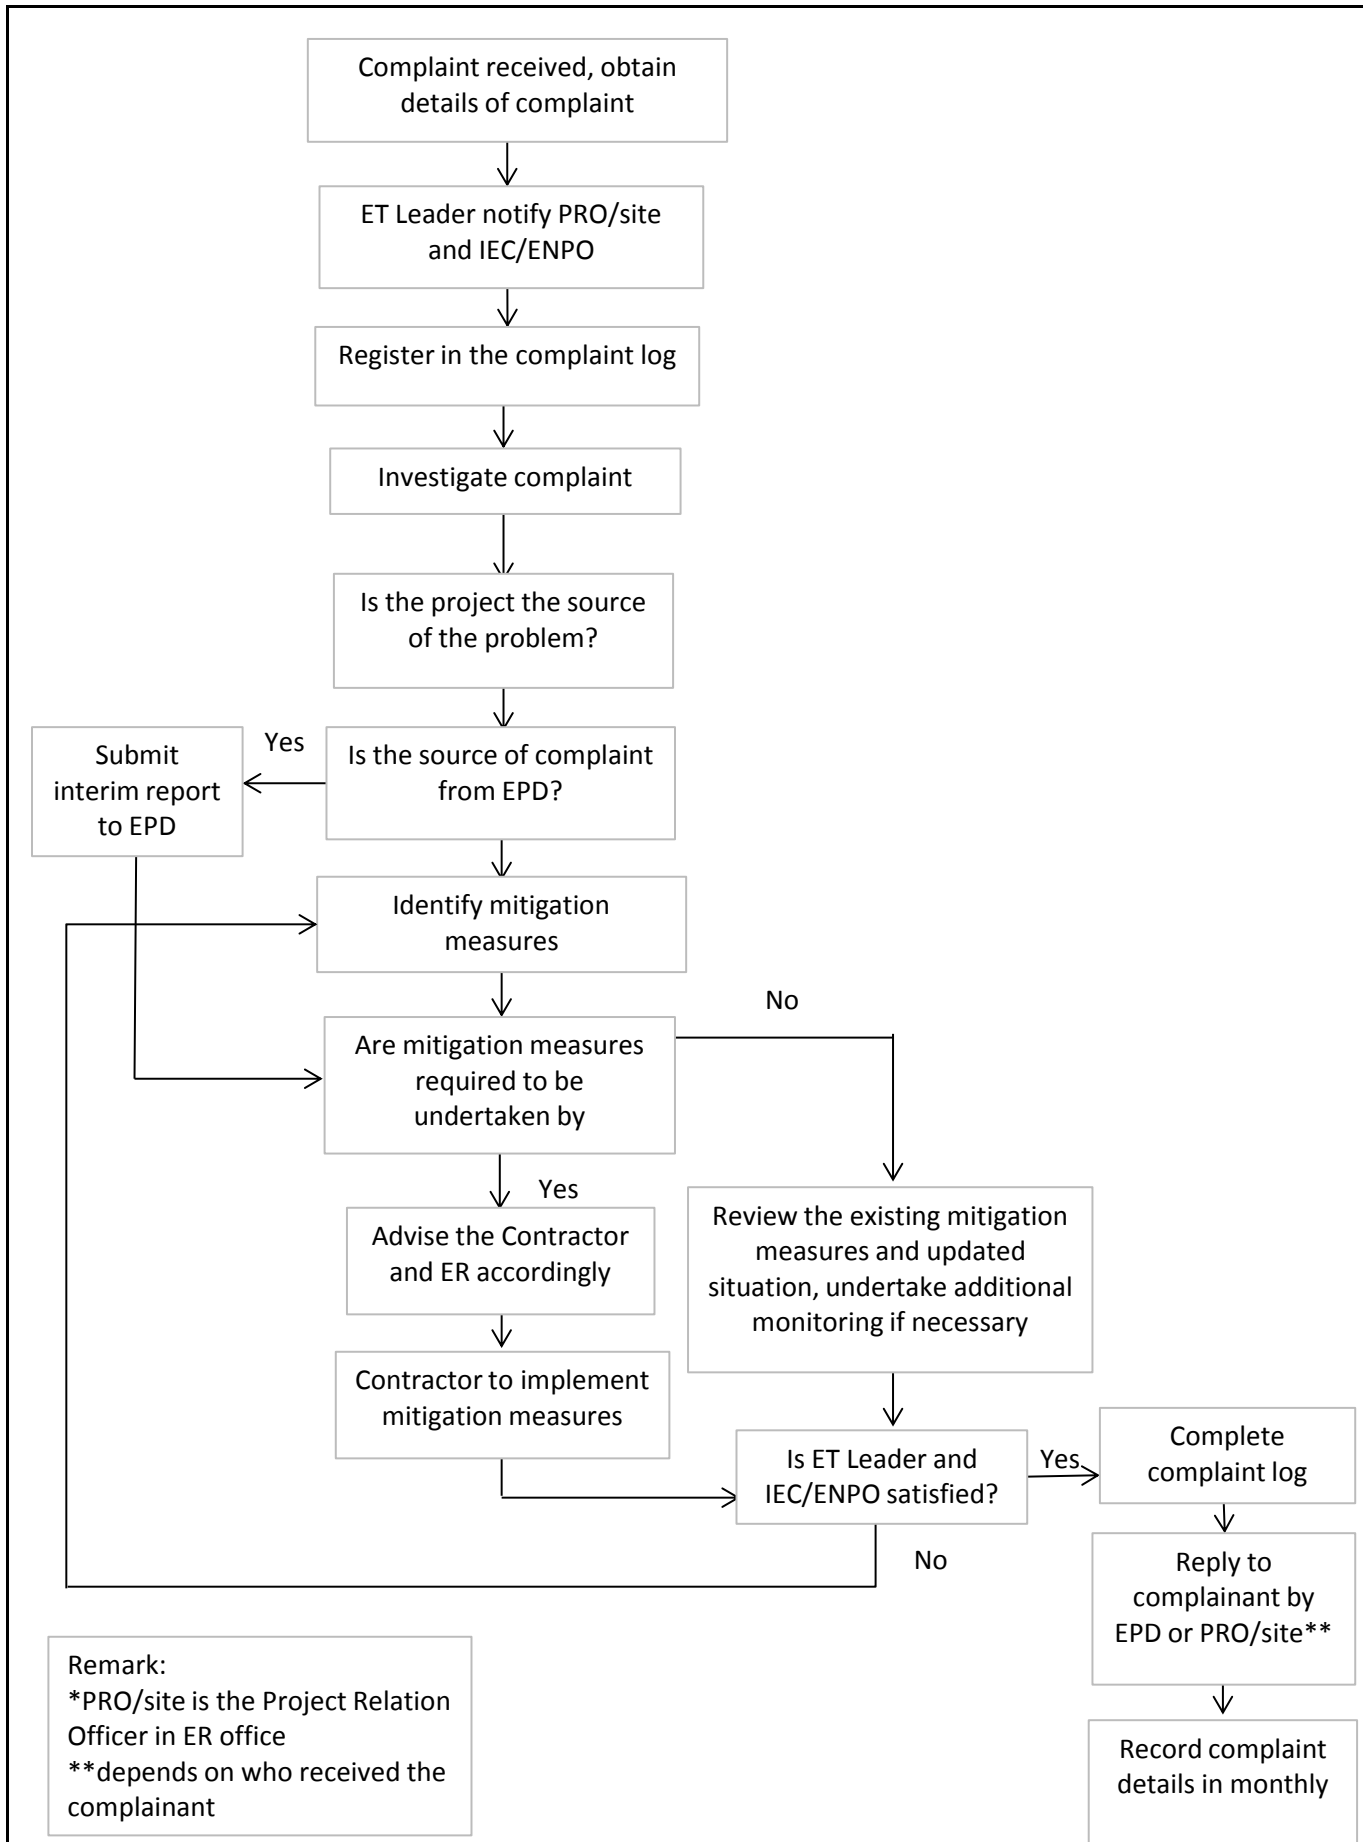

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

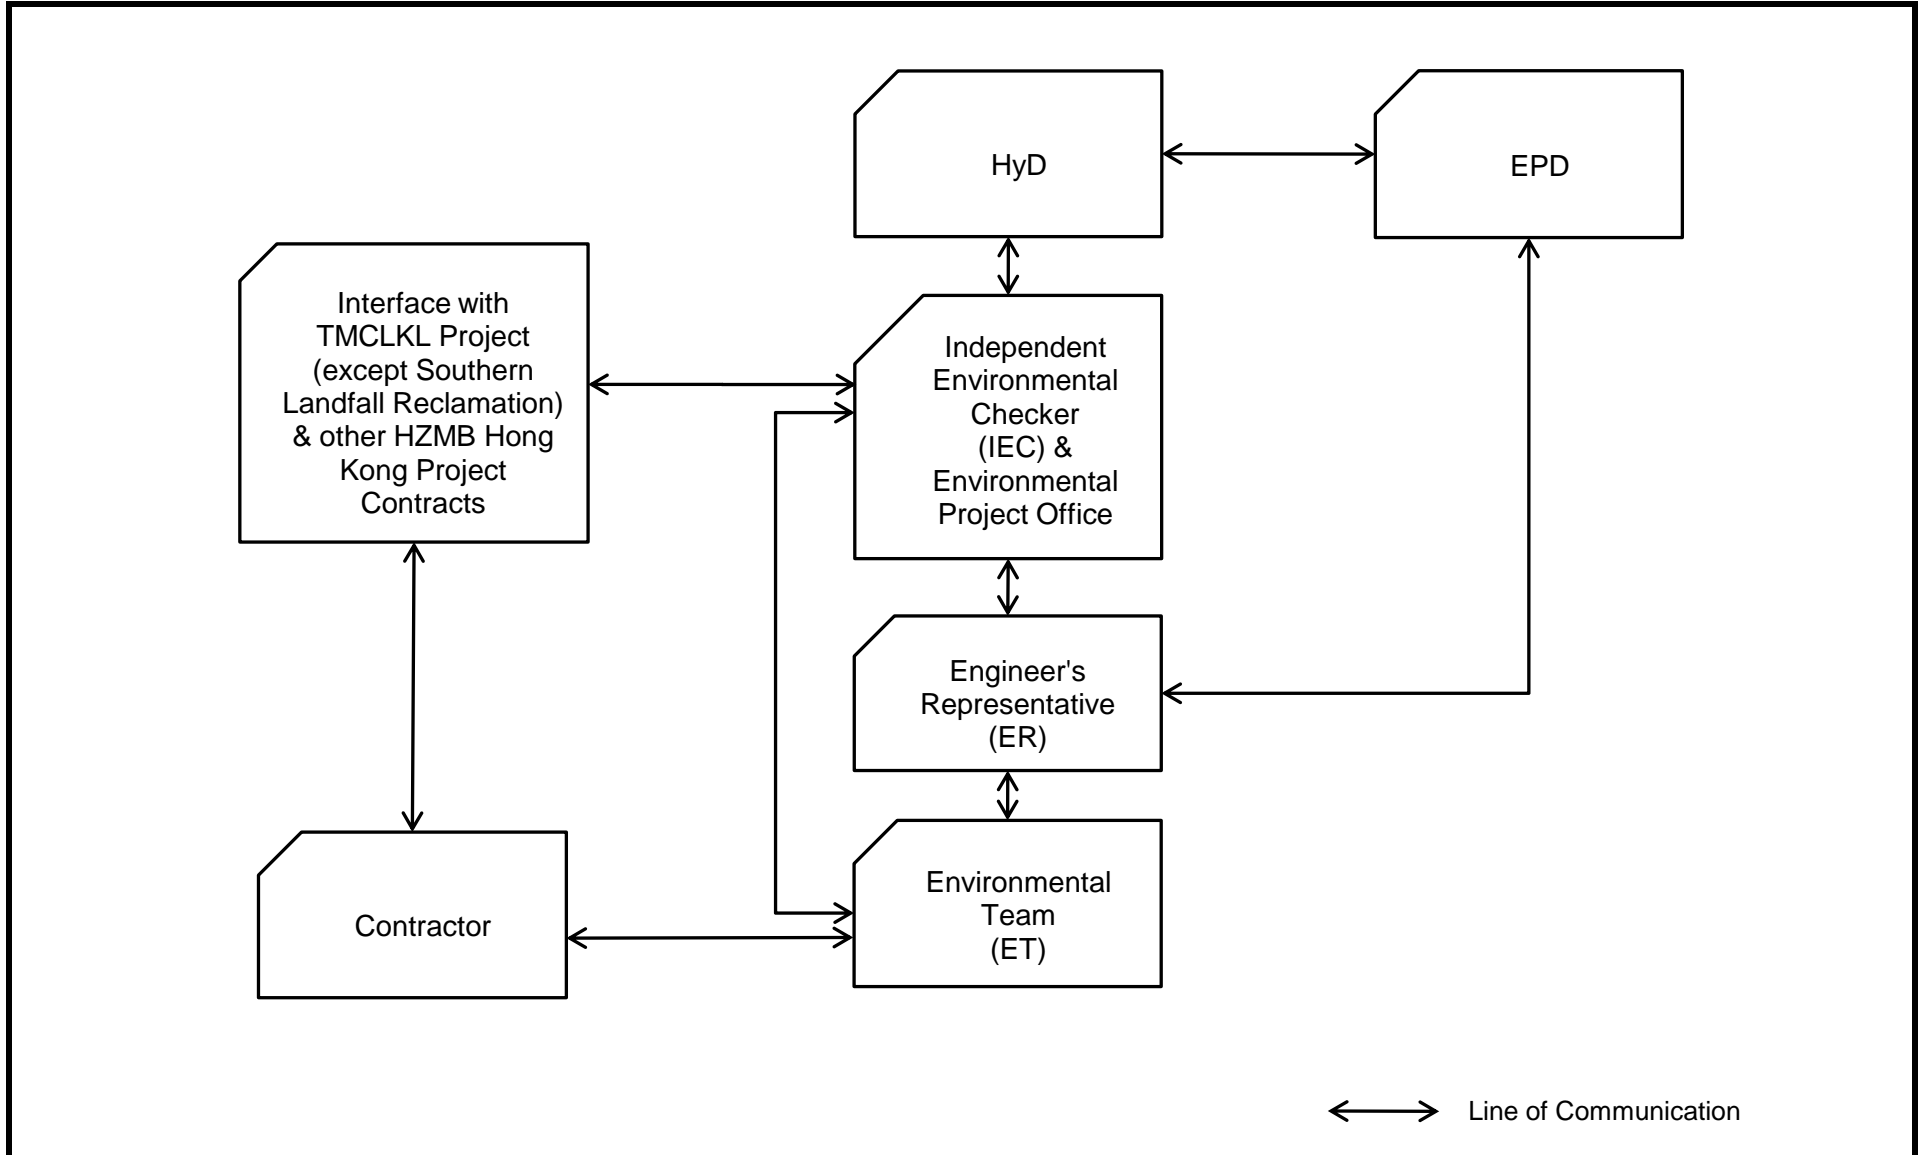

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2014				
						May 30	Jun 31	Jul 32	Aug 33	
29th Monthly Progress Report Status as on 21May2014 Ver.5										
Contract Key Dates										
Key Dates for achievement of Stages and completion of Sections										
G1040	KD-2, Achievement of Stage 2 (420days+EOT 2days, 24Jan2013)	0d		11-Jun-14*	-136d					
G1050	KD-3, Achievement of Stage 3 (730days+EOT 2days, 30Nov2013)	0d		01-Jun-14*	-182d					
G1063	KD-4, Completion of Section A Main Area (730days+EOT 0.5days, 29Nov2013) PCB Arc	0d		16-Jun-14*	-48d					
Work Zone, as defined in PS Clause 1.03(6)										
Portion A, B, C & E										
Seawall										
Ground Treatment										
Stone Columns for Rubble Mound Seawall by Marine Plant										
Portion C2a C113 - C117 5Cells 3,258Nos										
SC0A-	PC2A Stone Columns outermost C113 - C115 5cells 1,614nrs (19nrs/day) FTB17	165d	11-Nov-13 A	10-May-14 A						
Stone Columns Outside cellular Structures by Marine Plant										
Seawall Portion E1 at C068 - C091 24cells 6,428nrs										
C068 - C079										
SC0I	PE1 Stone Columns C068 - C078 Row 12-14 325nrs (8nrs/day) FTB16	45d	17-Mar-14 A	26-May-14	44d					
SC0I	PE1 Stone Columns C072 - C075 Row 01-11 769nrs (14nrs/day) FTB20	68d	21-Feb-14 A	30-May-14	40d					
SC0I	PE1 Stone Columns C077 - C077 Row 01-11 390nrs (6nrs/day) AP7	36d	13-Apr-14 A	08-May-14 A						
SC0I	PE1 Stone Columns C078 - C079 Row 01-11 780nrs (14nrs/day) FTB19	56d	07-Mar-14 A	23-May-14	86d					
C080 - C091										
SC0I	PE1 Stone Columns C081 - C083 Row 01-11 479nrs (14nrs/day) FTB18	34d	18-Apr-14 A	24-May-14	24d					
SC0I	PE1 Stone Columns C085 - C090 Row 01-11 284nrs (18nrs/day) FTB18	65d	07-Mar-14 A	30-May-14	18d					
SC0I	PE1 Stone Columns C079 - C091 Row 12-14 279nrs (6nrs/day) AP7	75d	21-Feb-14 A	10-May-14 A						
Stone Columns Inside cells by Land Plant 2,640nrs										
Seawall Portion B at K028 - K051 24cells 1,920nrs										
SCIB0	PB Stone Columns inside cells K044 - K046 136nrs (5nrs/day) LB-AP3	61d	15-Feb-14 A	22-May-14	-180d					
SCIB0	PB Stone Columns inside cells K047 - K050 267nrs (5nrs/day) LB-AP1	81d	21-Jan-14 A	22-May-14	-180d					
Seawall Portion E2 at K052 - C060 9cells 720nrs										
SCIE2	PE2 Stone Columns inside cells K052 - K055 320nrs (5nrs/day) LB-AP2	64d	21-Feb-14 A	30-May-14	19d					
SCIE2	PE2 Stone Columns inside cells K056 - C056 80nrs (3nrs/day) LB-BC1	16d	21-Mar-14 A	13-May-14 A						
SCIE2	PE2 Stone Columns inside cells K057 - C059 240nrs (3nrs/day) LB-BV1	80d	21-Feb-14 A	27-May-14	22d					
SCIE2	PE2 Stone Columns inside cells C061 - C062 240nrs (3nrs/day) LB-BV2	80d	21-Feb-14 A	27-May-14	22d					
Cellular Structures										
Cellular Main Cells 85cells										
Full Guide Frames Method 85cells										
Portion E1 C078 & C079 & Portion E2 C065 & C066 4cells										
CSE1	PE1 Cellular Structure C078 & C079 2cells Type_C 9,143m3	48d	01-Jul-14	20-Aug-14	-45d					
Connecting Arcs										
Portion E2 between K051/K052 to C066/C067 16arcs										
CAE2-	PE2 Connecting Arc C062/C063 - C066/C067 Seaside upper arcs splicing 5nrs (205)	31d	22-Apr-14 A	30-May-14	-105d					
CAE2-	PE2 Connecting Arc C063/C064 - C065/C066 Landside upper arcs splicing 3nrs (WC1)	18d	29-May-14	19-Jun-14	-32d					
CAE2-	PE2 Final backfill cellular cells & Arcs C063/C064, C064/C065, C065/C066 & C066/C067	7d	04-Jun-14	11-Jun-14	-107d					
Portion E1 between C073/C074 to C090/C091 18arcs										
CAE1-	PE1 Connecting Arc C084/C085 - C087/C088 Landside upper arcs splicing 4nrs (HF)	34d	07-Apr-14 A	21-May-14	-32d					
CAE1-	PE1 Connecting Arc C080/C081 - C086/C087 Seaside upper arcs splicing 7nrs (205)	65d	21-Mar-14 A	12-Jun-14	1d					



Hong Kong Boundary Corssing Facilities - Reclamation Works

Data Date :21-May-14

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2014			
						May 30	Jun 31	Jul 32	Aug 33
CAE1-	PE1 Connecting Arc C080/C081 - C083/C084 Landside upper arcs splicing 4nrs (HF)	24d	22-May-14	19-Jun-14	-32d				
CAE1-	PE1 Final backfill cellular cells & Arcs C080/C081 to C090/C091 Type_C 91,454.5 m3	22d	30-May-14	25-Jun-14	-5d				
CAE1-	PE1 Connecting Arc C072/C073 - C076/C077 Landside upper arcs splicing 5nrs (210)	44d	01-Apr-14 A	28-May-14	-32d				
CAE1-	PE1 Connecting Arc C072/C73 - C076/C077 Seaside upper arcs splicing 5nrs (WC1)	33d	29-May-14	08-Jul-14	-2d				
CAE1-	PE1 Connecting Arc C067/C068 - C071/C072 Landside upper arcs splicing 5nrs (401)	53d	21-Mar-14 A	25-Jun-14	-37d				
CAE1-	PE1 Connecting Arc C067/C068 - C071/C072 Seaside upper arcs splicing 5nrs (WC1)	30d	09-May-14 A	28-May-14	-2d				
CAE1-	PE1 Final backfill cellular cells & Arcs C077 to C066 Type_C 108,416m3	26d	13-Jun-14	14-Jul-14	-1d				
CAE1-	PE1 Completion of Cellular Cell at interface of TM-CLKL Tunnel	0d		14-Jul-14	357d				
Capping Beams		158d	15-Apr-14 A	01-Oct-14	17d				
Portion B between K028 to K056 Capping Beams		85d	15-Apr-14 A	23-Jun-14	-181d				
CB02E	PB Capping Beams structure K028 - K043 16-1=15cells 4days/cell	50d	15-Apr-14 A	07-Jun-14	-181d				
CB02E	PB Capping Beams structure K044 - K056 13cells 4days/cell	52d	29-Apr-14 A	23-Jun-14	-181d				
Portion E2 between K057 to C067 Capping Beams		44d	04-Jul-14	19-Aug-14	17d				
CBE2-	PE2 Capping Beams structure K057 to C062 6cells 4days/cell	24d	04-Jul-14	29-Jul-14	10d				
CBE2-	PE2 Capping Beams structure K063 to C064 2cells 4days/cell	8d	30-Jul-14	06-Aug-14	10d				
CBE2-	PE2 Capping Beams structure C065 to C067 3cells 4days/cell	12d	07-Aug-14	19-Aug-14	17d				
Portion C2a between C112 to C103 Capping Beams		31d	08-Jun-14	10-Jul-14	-64d				
CBC2c	PC2a Capping Beams structure C106 to C103 4cells 4days/cell	16d	24-Jun-14	10-Jul-14	-64d				
CBC2c	PC2a Capping Beams structure C112 to C107 6cells 4days/cell	24d	08-Jun-14	03-Jul-14	-57d				
Portion C2c between C102 to C091 Capping Beams		48d	11-Jul-14	31-Aug-14	10d				
CBC2c	PC2c Capping Beams structure C102 to C091 12cells 4days/cell	48d	11-Jul-14	31-Aug-14	10d				
Portion E1 between C090 to C074 Capping Beams		40d	20-Aug-14	01-Oct-14	17d				
CBE1-	PE1 Capping Beams structure C068 to C077 10cells 4days/cell	40d	20-Aug-14	01-Oct-14	17d				
Optimizing Rubble Mound Seawalls		60d	12-May-14 A	15-Jul-14	-50d				
Seawall Portion C2a at C117 - C113		60d	12-May-14 A	15-Jul-14	-50d				
RFC2a	PC2a at C117 - C113 Geotextile Type 1 above stone blanket 17,800m2	2d	12-May-14 A	13-May-14 A					
RFC2a	PC2a at C117 - C113 sound survey	2d	14-May-14 A	15-May-14 A					
RFC2a	PC2a at C117 - C113 settlement markers install	2d	16-May-14 A	17-May-14 A					
RFC2a	PC2a at C117 - C113 Filter Layer (Cat0 Fill 1m) under the Rubble Mound 23,430m3	6d	19-May-14 A	24-May-14	-104d				
RFC2a	PC2a at C117 - C113 Rockfill (Cat1) upto -3.0mPD 27,930m3	14d	25-May-14	08-Jun-14	-104d				
RFC2a	PC2a at C117 - C113 Sand Blanket behind upto -4.0mPD	2d	09-Jun-14	10-Jun-14	-104d				
RFC2a	PC2a at C117 - C113 Rockfill (Cat1), filter layer & geotextile +2.5mPD 21,060m3	12d	11-Jun-14	23-Jun-14	-104d				
RFC2a	PC2a at C117 - C113 Rockfill (Cat1) for platform upto +2.5mPD 19,530m3	10d	24-Jun-14	04-Jul-14	-78d				
RFC2a	PC2a at C117 - C113 Rockfill (Cat1 Fill) upto +6.0mPD & geotextile laying 7,980m3	4d	05-Jul-14	08-Jul-14	-62d				
RFC2a	PC2a at C117 - C113 UnderLayer (0mPD 12,600m3	6d	09-Jul-14	15-Jul-14	-50d				
Conforming Sloping Seawalls		146d	20-Apr-14 A	24-Sep-14	2d				
Geotextile		102d	27-Apr-14 A	14-Aug-14	-10d				
Seawall Portion C2a at C112 - C103 10cells		20d	01-May-14 A	22-May-14	-18d				
SGC2c	PC2a Geotextile at C112 - C103 10cells	20d	01-May-14 A	22-May-14	-18d				
Seawall Portion C2c at C102 - C091 12cells		24d	23-May-14	17-Jun-14	-15d				
SGC2c	PC2c Geotextile at C102 - C091 12cells	24d	23-May-14	17-Jun-14	-15d				
Seawall Portion E2 at K052 - C067 16cells		60d	27-Apr-14 A	30-Jun-14	-10d				
SGE2-	PE2 Geotextile at K052 - K062 11cells	11d	27-Apr-14 A	08-May-14 A					
SGE2-	PE2 Geotextile at K063 - K067 5cells	12d	18-Jun-14	30-Jun-14	-10d				
Seawall Portion E1 at C068 - C090 23cells		42d	01-Jul-14	14-Aug-14	-10d				
SGE1-	PE1 Geotextile at C090 - C080 11cells	22d	01-Jul-14	23-Jul-14	-10d				
SGE1-	PE1 Geotextile at C077 - C068 10cells	20d	24-Jul-14	14-Aug-14	-10d				
Rockfill		146d	20-Apr-14 A	24-Sep-14	2d				

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Hong Kong Boundary Corssing Facilities - Reclamation Works

Data Date :21-May-14

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2014			
						May 30	Jun 31	Jul 32	Aug 33
Seawall Portion B at K041 - K051									
RFB3-	PB Rockfill at K041 - K051 Rockfill 11cells	22d	20-Apr-14 A	13-May-14 A					
Seawall Portion C2a at C112 - C103 10cells									
RFC2-	PC2a Rockfill at C112 - C103 Rockfill 10cells	40d	05-May-14 A	16-Jun-14	-115d				
Seawall Portion C2c at C102 - C091 12cells									
RFC2-	PC2c Rockfill at C102 - C091 12cells	48d	18-Jun-14	07-Aug-14	-15d				
Seawall Portion E2 at K052 - C067 16cells									
RFE2-	PE2 Rockfill at C052 - C062 11cells	44d	14-May-14 A	30-Jun-14	-9d				
RFE2-	PE2 Rockfill at C063 - C067 5cells	20d	01-Jul-14	21-Jul-14	62d				
Seawall Portion E1 at C068 - C090 23cells									
RFE1-	PE1 Rockfill at C090 - C080 11cells	44d	08-Aug-14	24-Sep-14	-15d				
RFE1-	PE1 Rockfill at C077 - C068 10cells	50d	28-Jul-14	18-Sep-14	-10d				
Reclamation									
		202d	10-Mar-14 A	27-Sep-14	-73d				
Ground Treatment									
Geotextile									
Existing Seabed Below -5mPD									
Land Portion E2 Northern Part									
GERI	PE2 Geotextile for sand blanket Northern (seabed below -5mPD)	8d	01-May-14 A	31-May-14	-45d				
Sand Blankets									
Existing Seabed below -5mPD									
Land Portion E2 Northern Part									
SABF	Sand Blankets at PE2 71,000m3 5,000m3/day North-East	15d	02-Jun-14	17-Jun-14	-45d				
Existing Seabed Above -5mPD									
Land Portion E2 Southern Part									
SABF	Sand Blankets at PE2 142,000m3 5000m3/day South	28d	30-Apr-14 A	29-May-14	-43d				
Vertical Band Drains by Marine Plant									
Land Portion E2 Northern Part 84,746nrs									
VBDE	Vertical Band Drains 61,714nrs by marine plant at PE2 (750nrs/day)	84d	01-Apr-14 A	30-Jun-14	-45d				
Marine Fill									
Land Portion B									
Edge K013 - K27									
MFB1-	Marine Fill Type A Sand 100% at PB Edge at K013 - K027 380,000m3 10,000m3/day	31d	10-Apr-14 A	09-May-14 A					
Edge K028 - K054									
MFB3-	Marine Fill Type A Sand 100% stg2 at PB Edge at K028 - K034 140,000m3 27,000m3/d	6d	06-May-14 A	06-Jun-14	-204d				
MFB3-	Marine Fill Type A Sand 100% stg2 at PB Edge at K035 - K040 106,000m3 27,000m3/d	5d	23-May-14	27-May-14	-204d				
MFB4-	Marine Fill Type A Sand 100% stg3 at PB Edge at K041 - K048 200,000m3 40,000m3/d	5d	28-May-14	01-Jun-14	-204d				
MFB4-	Marine Fill Type A Sand 100% stg3 at PB Edge at K049 - K054 270,000m3 40,000m3/d	5d	02-Jun-14	06-Jun-14	-204d				
Main Area									
MFB5-	Marine Fill Type A Sand 100% stg4 at PB Main South 350,000m3 40,000m3/day	17d	21-Apr-14 A	07-May-14 A					
MFB6-	Marine Fill Type A Sand 100% stg5 at PB Main North 240,000m3 10,000m3/day	24d	08-May-14 A	29-May-14	-196d				
Land Portion C1b									
MFC1b	Marine Fill Type A Sand 70% at PC1b east 454,612m3 20,000m3/day	23d	26-Jul-14	19-Aug-14	-157d				
Land Portion C2a									
MFC2a	Marine Fill Type A Sand 70% at PC2a 730,287m3 20,000m3/day	36d	20-Aug-14	27-Sep-14	-157d				
Land Portion E2									
MFE2-	Start PE2 after Marine Fill Type A Sand 100% at PC1b	0d	20-Aug-14	20-Aug-14	-60d				
Vertical Band Drains by Land Plant									
Land Portion A 233,590nrs									
		83d	10-Mar-14 A	31-May-14	-230d				

Remaining Level of Effort Remaining Work
 Actual Level of Effort Critical Remaining Work
 Actual Work Milestone

Hong Kong Boundary Corssing Facilities - Reclamation Works

Data Date :21-May-14

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2014			
						May 30	Jun 31	Jul 32	Aug 33
VBDA0-	Vertical Band Drains 39,000nrs by Land plant at PA C127 - C134 w CLP substation 500i	83d	10-Mar-14 A	31-May-14	-230d	[Gantt bar: 10-Mar-14 to 31-May-14]			
Land Portion B 304,328nrs		69d	01-Apr-14 A	15-Jul-14	-210d	[Gantt bar: 01-Apr-14 to 15-Jul-14]			
Edge K13 - K27 26,798nrs by Land		45d	01-Jun-14	15-Jul-14	-210d	[Gantt bar: 01-Jun-14 to 15-Jul-14]			
VBDBI	Vertical Band Drains by land plant at PB Edge K013 - K027 26,798nrs 650nrs/day (6VP -	45d	01-Jun-14	15-Jul-14	-210d	[Gantt bar: 01-Jun-14 to 15-Jul-14]			
Edge K28 - K54 76,000nrs by Land		69d	01-Apr-14 A	23-Jun-14	-200d	[Gantt bar: 01-Apr-14 to 23-Jun-14]			
VBDBI	Vertical Band Drains by land plant at PB Corridor 12,000nrs 4,000nrs/day (13HP)	4d	06-May-14 A	09-May-14 A		[Gantt bar: 06-May-14 to 09-May-14]			
VBDBI	Vertical Band Drains by land plant at PB Edge K028 - K034 38,520nrs 4,000nrs/day (13HP)	10d	10-May-14 A	04-Jun-14	-200d	[Gantt bar: 10-May-14 to 04-Jun-14]			
VBDBI	Vertical Band Drains by land plant at PB Edge K035 - K040 12,000nrs 4,000nrs/day (13HP)	3d	05-Jun-14	07-Jun-14	-200d	[Gantt bar: 05-Jun-14 to 07-Jun-14]			
VBDBI	Vertical Band Drains by land plant at PB Edge K041 - K048 44,000nrs 4,000nrs/day	11d	08-Jun-14	18-Jun-14	-200d	[Gantt bar: 08-Jun-14 to 18-Jun-14]			
VBDBI	Vertical Band Drains by marine plant at PB Edge K049 - K054 30,000nrs 750nrs/day	40d	01-Apr-14 A	20-May-14 A		[Gantt bar: 01-Apr-14 to 20-May-14]			
VBDBI	Vertical Band Drains by land plant at PB Edge K049 - K054 20,000nrs 4,000nrs/day	5d	19-Jun-14	23-Jun-14	-200d	[Gantt bar: 19-Jun-14 to 23-Jun-14]			
Main Area 201,530nrs by Land		13d	10-May-14 A	01-Jun-14	-186d	[Gantt bar: 10-May-14 to 01-Jun-14]			
VBDBI	Vertical Band Drains by land plant at PB Main South 20,000nrs 4,000nrs/day (13HP)	5d	10-May-14 A	20-May-14 A		[Gantt bar: 10-May-14 to 20-May-14]			
VBDBI	Vertical Band Drains by land plant at PB Main North 15,000nrs 4,000nrs/day (13HP)	4d	20-May-14 A	01-Jun-14	-186d	[Gantt bar: 20-May-14 to 01-Jun-14]			
Land Portion C1a 17,700nrs by Land		28d	16-Jul-14	12-Aug-14	-27d	[Gantt bar: 16-Jul-14 to 12-Aug-14]			
VBDC1	Vertical Band Drains 17,700nrs by land plant at PC1a 650nrs/day (6VP + 6HP(NS))	28d	16-Jul-14	12-Aug-14	-27d	[Gantt bar: 16-Jul-14 to 12-Aug-14]			
Land Portion C1b 98,260nrs by Land		63d	24-Jun-14	25-Aug-14	-153d	[Gantt bar: 24-Jun-14 to 25-Aug-14]			
VBDC1	Vertical Band Drains 18,000nrs by land plant at PC1b west 3,000nrs/day (11HP)	6d	24-Jun-14*	29-Jun-14	-108d	[Gantt bar: 24-Jun-14 to 29-Jun-14]			
VBDC1	Vertical Band Drains 18,000nrs by land plant at PC1b east 3,000nrs/day (11HP)	6d	20-Aug-14	25-Aug-14	-153d	[Gantt bar: 20-Aug-14 to 25-Aug-14]			
Earthwork Fill		76d	21-May-14	04-Aug-14	-187d	[Gantt bar: 21-May-14 to 04-Aug-14]			
Land Portion A		61d	21-May-14	20-Jul-14	-172d	[Gantt bar: 21-May-14 to 20-Jul-14]			
EFA0-0	Allow fill up above +2.5mPD by Vane Shear Test	0d	21-May-14		-124d	[Milestone: 21-May-14]			
EFA0-0	Allow to Earthwork Fill at PA A2	0d	21-May-14*		-201d	[Milestone: 21-May-14]			
EFA0-0	Earthwork Fill Type D Sand 100% at PA at C122 - C126 other area 202,000m3 12,000rr	17d	20-Jun-14*	07-Jul-14	-210d	[Gantt bar: 20-Jun-14 to 07-Jul-14]			
EFA0-0	Earthwork Fill Type D Sand 100% at PA at C122 - C126 Edge Area 146,046m3 12,000rr	12d	08-Jul-14	20-Jul-14	-155d	[Gantt bar: 08-Jul-14 to 20-Jul-14]			
EFA0-0	Earthwork Fill Type D Sand 100% at PA at C127 - C134 Edge Area 202,097m3 12,000rr	17d	02-Jun-14	19-Jun-14	-210d	[Gantt bar: 02-Jun-14 to 19-Jun-14]			
Land Portion B		59d	07-Jun-14	04-Aug-14	-210d	[Gantt bar: 07-Jun-14 to 04-Aug-14]			
Edge K013 - K027		20d	16-Jul-14	04-Aug-14	-210d	[Gantt bar: 16-Jul-14 to 04-Aug-14]			
EFB0-	Earthwork Fill Type D Sand 100% at PB Edge at K013 - K027 400,000m3 20,000m3/day	20d	16-Jul-14	04-Aug-14	-210d	[Gantt bar: 16-Jul-14 to 04-Aug-14]			
Edge K028 - K054		24d	08-Jun-14	01-Jul-14	-184d	[Gantt bar: 08-Jun-14 to 01-Jul-14]			
EFB0-	Earthwork Fill Type D Sand 100% at PB Edge at K028 - K034 186,000m3 40,000m3/day	5d	12-Jun-14	16-Jun-14	-204d	[Gantt bar: 12-Jun-14 to 16-Jun-14]			
EFB0-	Earthwork Fill Type D Sand 100% at PB Edge at K035 - K040 106,000m3 40,000m3/day	3d	17-Jun-14	19-Jun-14	-204d	[Gantt bar: 17-Jun-14 to 19-Jun-14]			
EFB0-	Earthwork Fill Type D Sand 100% at PB Edge at K041 - K048 160,000m3 40,000m3/day	4d	24-Jun-14	27-Jun-14	-204d	[Gantt bar: 24-Jun-14 to 27-Jun-14]			
EFB0-	Earthwork Fill Type D Sand 100% at PB Edge at K041 - K048 80,000m3 10,000m3/day	8d	08-Jun-14	15-Jun-14	-176d	[Gantt bar: 08-Jun-14 to 15-Jun-14]			
EFB0-	Earthwork Fill Type D Sand 100% at PB Edge at K049 - K054 160,000m3 40,000m3/day	4d	28-Jun-14	01-Jul-14	-204d	[Gantt bar: 28-Jun-14 to 01-Jul-14]			
EFB0-	Earthwork Fill Type D Sand 100% at PB Edge at K049 - K054 80,000m3 10,000m3/day	8d	16-Jun-14	23-Jun-14	-176d	[Gantt bar: 16-Jun-14 to 23-Jun-14]			
Main Area		17d	07-Jun-14	23-Jun-14	-204d	[Gantt bar: 07-Jun-14 to 23-Jun-14]			
EFB0-	Earthwork Fill Type D Sand 100% at PB Main South 190000m3 40,000m3/day	5d	07-Jun-14	11-Jun-14	-204d	[Gantt bar: 07-Jun-14 to 11-Jun-14]			
EFB0-	Earthwork Fill Type D Sand 100% at PB Main North 135,000m3 40,000m3/day	4d	20-Jun-14	23-Jun-14	-204d	[Gantt bar: 20-Jun-14 to 23-Jun-14]			
Surcharge		304d	05-Feb-14 A	05-Dec-14	-45d	[Gantt bar: 05-Feb-14 to 05-Dec-14]			
Temporary Jettys		63d	17-Jun-14	19-Aug-14	-147d	[Gantt bar: 17-Jun-14 to 19-Aug-14]			
2nd Temporary Jetty at C101		51d	17-Jun-14	07-Aug-14	-135d	[Gantt bar: 17-Jun-14 to 07-Aug-14]			
TP20010	Footing at Land - Place Steel Bridge precast footing and anchor block on	5d	17-Jun-14	21-Jun-14	-100d	[Gantt bar: 17-Jun-14 to 21-Jun-14]			
TP20020	Marine Piling 10nrs	10d	08-Jul-14	18-Jul-14	-118d	[Gantt bar: 08-Jul-14 to 18-Jul-14]			
TP20030	Installation of Dolphins 2nrs	2d	19-Jul-14	21-Jul-14	-108d	[Gantt bar: 19-Jul-14 to 21-Jul-14]			
TP20040	Installation of main pier	2d	22-Jul-14	23-Jul-14	-108d	[Gantt bar: 22-Jul-14 to 23-Jul-14]			
TP20050	Installation of steel bridge from Jetty to the land footing	2d	24-Jul-14	25-Jul-14	-108d	[Gantt bar: 24-Jul-14 to 25-Jul-14]			
TP20060	Assembly of conveyor	10d	23-Jun-14	04-Jul-14	-100d	[Gantt bar: 23-Jun-14 to 04-Jul-14]			

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ ◆ Milestone

Hong Kong Boundary Corssing Facilities - Reclamation Works

Data Date :21-May-14

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2014			
						May 30	Jun 31	Jul 32	Aug 33
TP20070	Installation of conveyor	2d	26-Jul-14	28-Jul-14	-108d				
TP20080	Installation of accessory parts	2d	29-Jul-14	30-Jul-14	-108d				
TP20090	Trial testing	5d	31-Jul-14	05-Aug-14	-108d				
TP20100	Certification for the System	1d	06-Aug-14	06-Aug-14	-108d				
TP20110	Start Operation of unloading public fill at C101	0d	07-Aug-14		-135d				
3rd Temporary Jetty at C105		57d	23-Jun-14	19-Aug-14	-147d				
TP30010	Footing at Land - Place Steel Bridge precast footing and anchor block on	5d	23-Jun-14	27-Jun-14	-95d				
TP30020	Marine Piling 10nrs	10d	19-Jul-14	30-Jul-14	-118d				
TP30030	Installation of Dolphins 2nrs	2d	31-Jul-14	01-Aug-14	-118d				
TP30040	Installation of main pier	2d	02-Aug-14	04-Aug-14	-118d				
TP30050	Installation of steel bridge from Jetty to the land footing	2d	05-Aug-14	06-Aug-14	-118d				
TP30060	Assembly of conveyor	10d	05-Jul-14	16-Jul-14	-100d				
TP30070	Installation of conveyor	2d	07-Aug-14	08-Aug-14	-118d				
TP30080	Installation of accessory parts	2d	09-Aug-14	11-Aug-14	-118d				
TP30090	Trial testing	5d	12-Aug-14	16-Aug-14	-118d				
TP30100	Certification for the System	1d	18-Aug-14	18-Aug-14	-118d				
TP30110	Start Operation of unloading public fill at C105	0d	19-Aug-14		-147d				
5th Temporary Jetty at K053		36d	25-Jun-14	31-Jul-14	-130d				
TP50010	Footing at Land - Place Steel Bridge precast footing and anchor block on	5d	02-Jul-14	07-Jul-14	-118d				
TP50020	Marine Piling 10nrs	10d	25-Jun-14	07-Jul-14	-118d				
TP50030	Installation of Dolphins 2nrs	2d	08-Jul-14	09-Jul-14	-99d				
TP50040	Installation of main pier	2d	10-Jul-14	11-Jul-14	-99d				
TP50050	Installation of steel bridge from Jetty to the land footing	2d	12-Jul-14	14-Jul-14	-99d				
TP50060	Assembly of conveyor	10d	08-Jul-14*	18-Jul-14	-103d				
TP50070	Installation of conveyor	2d	19-Jul-14	21-Jul-14	-103d				
TP50080	Installation of accessory parts	2d	22-Jul-14	23-Jul-14	-103d				
TP50090	Trial testing	5d	24-Jul-14	29-Jul-14	-103d				
TP50100	Certification for the System	1d	30-Jul-14	30-Jul-14	-103d				
TP50110	Start Operation of unloading public fill at K053	0d	31-Jul-14		-130d				
Flat Barges for unloading		0d	21-May-14	21-May-14	-159d				
FB10010	Flat Barge for unloading at C132	0d	21-May-14*		-159d				
Portion A Surcharge		304d	05-Feb-14 A	05-Dec-14	-220d				
Main Reclamation Areas		304d	05-Feb-14 A	05-Dec-14	-220d				
A1 PCB East		124d	05-Feb-14 A	08-Jun-14	-40d				
SURAI	Surcharge Period at PA PCB East 3.5mths (8-4.5=3.5mths)	105d	05-Feb-14 A	31-May-14	-128d				
SURAI	Sand Surcharge Removal at PA PCB East 126,794m3 20,000m3/day	7d	02-Jun-14	08-Jun-14	-115d				
SURAI	Completion of PA PCB East	0d		08-Jun-14	-40d				
A1 PCB West		113d	24-Feb-14 A	16-Jun-14	-48d				
SURAI	Surcharge Period at PA PCB West 3.5mths (8-4.5=3.5mths)	105d	24-Feb-14 A	08-Jun-14	-124d				
SURAI	Sand Surcharge Removal at PA PCB West 126,794m3 20,000m3/day	7d	09-Jun-14	16-Jun-14	-115d				
SURAI	Completion of PA PCB West	0d		16-Jun-14	-48d				
A2		151d	08-Jul-14	05-Dec-14	-231d				
SURAI	Surcharge Laying upto +11.5mPD & compaction upto +8.5mPD on Main Area at PA 285,	29d	08-Jul-14	07-Aug-14	-210d				
SURAI	Surcharge Period on Main Area at PA 6mth (8-2-1-1=4mths)	120d	08-Aug-14	05-Dec-14	-231d				
at C127 - C134 for Power Substation Area		124d	20-Jun-14	21-Oct-14	-179d				
SURAI	Sand Surcharge Laying upto +11.5mPD & compaction upto +8.5mPD on Main Area at P	4d	20-Jun-14	23-Jun-14	-162d				
SURAI	Surcharge Period on Main Area at PA CLP substation 6mth (8-2-1-1=4mths)	120d	24-Jun-14	21-Oct-14	-179d				
Edge Areas		91d	20-Jun-14	18-Sep-14	-166d				



Hong Kong Boundary Corssing Facilities - Reclamation Works

Data Date :21-May-14

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2014					
						May 30	Jun 31	Jul 32	Aug 33		
at C125 - C119											
SUEA	Pause Period on Edge Area at PA 2mths	60d	21-Jul-14	18-Sep-14	-171d						
at C134 - C126											
SUEA	Pause Period on Edge Area at PA 2mths	60d	20-Jun-14	18-Aug-14	-147d						
SUEA	Surcharge Laying & compaction upto 8.5mPD on Edge Area at PA 107,295m3 10,000m3	11d	19-Aug-14	30-Aug-14	-136d						
Land Portion B											
Edge Areas											
at K013 - K027											
SUEB	Surcharge Period 2mths after Fill upto +5.5mPD at PB at K013-K027	60d	05-Aug-14	03-Oct-14	-210d						
at K028 - K034											
SUEB	Sand Surcharge Laying up to 8.5mPD on Edge Area at PB at K028 - K034 100,000m3 4	3d	05-Jul-14	07-Jul-14	-185d						
SUEB	Surcharge Period 1st stage on Edge Area at PB 2mths (4.5-2.5=2mths)	60d	08-Jul-14	05-Sep-14	-196d						
at K035 - K040											
SUEB	Sand Surcharge Laying up to 8.5mPD on Edge Area at PB at K035 - K040 60,000m3 40	2d	08-Jul-14	09-Jul-14	-185d						
SUEB	Surcharge Period 1st stage on Edge Area at PB 2mths (4.5-2.5=2mths)	60d	10-Jul-14	07-Sep-14	-195d						
at K041 - K048											
SUEB	Sand Surcharge Laying up to 8.5mPD on Edge Area at PB at K041 - K051 160,000m3 4	4d	10-Jul-14	14-Jul-14	-179d						
SUEB	Additional GI Works by Other Contractors HY/2010/07	30d	15-Jul-14	18-Aug-14	-140d						
SUEB	Surcharge Period 1st stage on Edge Area at PB 2mths (4.5-2.5=2mths)	60d	15-Jul-14	12-Sep-14	-198d						
at K049 - K054											
SUEB	Sand Surcharge Laying up to 8.5mPD on Edge Area at PB at K049 - K054 160,000m3 4	4d	15-Jul-14	18-Jul-14	-178d						
SUEB	Additional GI Works by Other Contractors HY/2010/07	30d	19-Jul-14	22-Aug-14	-140d						
SUEB	Surcharge Period 1st stage on Edge Area at PB 2mths (4.5-2.5=2mths)	60d	19-Jul-14	16-Sep-14	-197d						
Reclamation Areas											
at Main 1											
SURB	Sand Surcharge Laying upto top on Main Reclamation Area at PB South 110,000m3 40,	3d	02-Jul-14*	04-Jul-14	-185d						
SURB	Surcharge Period on Main Reclamation Area at PB 6mths (7-3=4mths)	120d	05-Jul-14	01-Nov-14	-11d						
at Main 2											
SURB	Sand Surcharge Laying upto top on Main Reclamation Area at PB K041 - K051 267,000r	7d	19-Jul-14	25-Jul-14	-157d						
SURB	Surcharge Period on Main Reclamation Area at PB 6mths (7-3=4mths)	120d	26-Jul-14	22-Nov-14	-32d						
Geotechnical Instrumentation Works											
Geotechnical Instrumentation Works for Seawalls											
Cluster Type SD 26hrs Instrumentation and CPT Cluster behind cells											
Portion B											
SD-01 K014											
CTSI	Installation of SD-01 (K014) PB	13d	14-May-14 A	28-May-14	-57d						
SD-02 K019											
CTSI	Installation of SD-02 (K019) PB	30d	12-May-14 A	16-Jun-14	-57d						
SD-03 K023											
CTSI	Installation of SD-03 (K023) PB	30d	12-May-14 A	16-Jun-14	-57d						
SD-06 K038											
CTSI	Installation of SD-06 (K038) PB	30d	21-Mar-14 A	28-May-14	-124d						
SD-07 K042											
CTSI	Installation of SD-07 (K042) PB	30d	22-Apr-14 A	28-May-14	-124d						
SD-08 K047											
CTSI	Installation of SD-08 (K047) PB	30d	03-Jun-14	08-Jul-14	-140d						
SD-09 K051											
CTSI	Installation of SD-09 (K051) PB	30d	07-Jun-14	12-Jul-14	-144d						

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ ◆ Milestone

Hong Kong Boundary Corssing Facilities - Reclamation Works

Data Date :21-May-14

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2014			
						May 30	Jun 31	Jul 32	Aug 33
Cluster Type SE 26nrs Surface movement marker cluster at top of cell and sloping seawall									
CTSE-C	Installation of SE-01 (K017) PB	7d	12-May-14 A	19-May-14 A	65d				
CTSE-C	Installation of SE-02 (K021) PB	7d	12-May-14 A	19-May-14 A					
CTSE-C	Installation of SE-03 (K026) PB	7d	12-May-14 A	19-May-14 A					
CTSE-C	Installation of SE-07 (K046) PB	7d	03-Jun-14	10-Jun-14	-147d				
CTSE-C	Installation of SE-08 (K049) PB	7d	07-Jun-14	14-Jun-14	-151d				
CTSE-C	Installation of SE-09 (K052) PE2	7d	14-May-14 A	21-May-14	48d				
CTSE-1	Installation of SE-10 (C059) PE2	7d	14-May-14 A	21-May-14	48d				
CTSE-1	Installation of SE-11 (C064) PE2	7d	02-Jul-14	09-Jul-14	63d				
CTSE-1	Installation of SE-12 (C069) PE2	7d	28-Jul-14	04-Aug-14	70d				
CTSE-1	Installation of SE-13 (C071) PE1	7d	28-Jul-14	04-Aug-14	70d				
CTSE-1	Installation of SE-14 (C077) PE1	7d	08-Aug-14	15-Aug-14	31d				
CTSE-1	Installation of SE-15 (C079) PE1	7d	08-Aug-14	15-Aug-14	31d				
CTSE-1	Installation of SE-16 (C082) PE1	7d	08-Aug-14	15-Aug-14	31d				
CTSE-1	Installation of SE-17 (C087) PE1	7d	08-Aug-14	15-Aug-14	31d				
CTSE-1	Installation of SE-18 (C092) PC2c	7d	18-Jun-14	25-Jun-14	108d				
CTSE-1	Installation of SE-19 (C097) PC2c	7d	18-Jun-14	25-Jun-14	90d				
CTSE-2	Installation of SE-20 (C102) PC2a	14d	05-May-14 A	21-May-14	-15d				
CTSE-2	Installation of SE-21 (C106) PC2a	14d	05-May-14 A	21-May-14	-15d				
CTSE-2	Installation of SE-22 (C111) PC2a	14d	05-May-14 A	21-May-14	-15d				
CTSE-2	Installation of SE-23 (C116) PC2a	14d	05-May-14 A	21-May-14	-15d				
Geotechnical Instrumentation Works for Reclamation RA & RB									
RA									
CTRA-C	Installation of RA 9sets at PB	7d	07-Jun-14	14-Jun-14	818d				
CTRA-C	Installation of RA 8sets at PC1a	7d	02-May-14 A	10-May-14 A					
CTRA-C	Installation of RA 6sets at PC1b	7d	20-Aug-14	27-Aug-14	-113d				
RB									
SMT1-C	Installation of RB at PB	7d	19-Jun-14	26-Jun-14	808d				
SMT1-C	Installation of RB at PC1a	7d	02-May-14 A	10-May-14 A					
SMT1-C	Installation of RB at PC1b	7d	20-Aug-14	27-Aug-14	-113d				
Settlement Marker Type 2									
SMT2-C	M2 - Installation of Settlement Marker Type2 at PB	7d	29-May-14	06-Jun-14	825d				
SMT2-C	M2 - Installation of Settlement Marker Type2 at PC1a	7d	02-May-14 A	10-May-14 A					
SMT2-C	M2 - Installation of Settlement Marker Type2 at PC1b	7d	20-Aug-14	27-Aug-14	-113d				
Portion D									
Submission									
Design Submission									
Stability Analysis and Settlement Assessment for Vertical Seawall w No Dredging									
PD-DGN	Stability Analysis and settlement assessment for vertical seawall with no dredging	0d		21-May-14*	1019d				
Stability Analysis and Settlement Assessment for Sloping Seawall w No Dredging									
PD-DGN	Stability Analysis and Settlement Assessment for Sloping seawall with no dredging	0d		21-May-14*	1019d				
Settlement Assessment for Culverts C1 - C4 w No Dredging									
PD-DGN	Settlement assessment for box culverts C1 - C4 with no dredging	0d		21-May-14*	1019d				
Structural Analysis for Culverts C1 - C4 w Precast Method									
PD-DGN	Structural analysis for Box Culverts C1 - C4 with Precast Method	0d		21-May-14*	18d				
Drainage Impact Assessment & Temporary Diversion (stg2 - for construction of box culver									
PD-DGN	Drainage Impact Assessment and Temporary Diversion (stage 2 - for construction of box	0d		21-May-14*	18d				
Settlement Assessment for Box Culvert EC1									
PD-DGN	Settlement Assessment for Box Culvert EC1	0d		21-May-14	18d				

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ ◆ Milestone

Hong Kong Boundary Corssing Facilities - Reclamation Works

Data Date :21-May-14

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2014			
						May 30	Jun 31	Jul 32	Aug 33
PD-DGN	Settlement Assessment for Box culvert EC1 Submission 1st	0d		21-May-14*	18d				
Structural Analysis for Box Culvert EC1 w Precast & Cast in-situ Method									
PD-DGN	Structural Analysis for Box culvert EC1 with Precast and Cast in-situ Method	0d	21-May-14	21-May-14	18d				
Detailed General Arrangement & RC drawings for C1 to C4 w Precast Method									
PD-DGN	Detailed General Arrangement and RC drawings for Box culverts C1 to C4 with Precast	0d	21-May-14	21-May-14	18d				
Detailed General Arrangement & RC drawings for EC1 w Precast & Cast insitu Methods									
PD-DGN	Detailed General Arrangement and RC drawings for Box Culverts EC1 with Precast and	0d	21-May-14	21-May-14	1019d				
Precast Yard for Seawall Blocks & Culverts									
Culverts									
PD-PY-01	Precast Yard Setup	92d	01-Mar-14 A	31-May-14	-92d				
PD-PY-02	Commencement of Precast Box Culvert	0d	01-Jul-14*		-122d				
PD-PY-02	Precast C1 6nrs	60d	01-Jul-14	29-Aug-14	-122d				
PD-PY-02	Precast EC1 10nrs	60d	31-Jul-14	28-Sep-14	-122d				
Site Construction									
Seawall Construction									
Access at Portion D									
Existing Road to Portion D									
AA0140	Set up the TTA (Stage 3 and Stage 4) for access opening	2d	19-May-14 A	20-May-14 A					
Construction of Temporary Bridge									
AA1070	PD - Access Road from AA for delivery of public fill material	0d	21-May-14*		-171d				
Temporary Access to Portion A									
A1080	PD Construction of Temporary Access to PA	61d	01-Apr-14 A	31-May-14	-182d				
A1085	PD Provide Access to PA	0d	01-Jun-14		-182d				
WaterMain Construction									
A30010	PD - Temp Watermain Construction approved by AA & WSD	24d	25-Apr-14 A	07-Jun-14	-53d				
A30020	PD - Temp Watermain Construction along Access	60d	08-Jun-14	06-Aug-14*	-67d				
Reclamation Above +2.5mPD									
West1 (South CH 0 -100 & North CH6136 - 6000)									
A1633	PD - Earthwork Fill upto + 5.5 mPD at West1 47,269m3 5,000m3/day	25d	14-Apr-14 A	11-May-14 A					
West2 (South CH 100 -225 & North CH6000 - 5900)									
A2120	PD - Earthwork Fill upto + 5.5 mPD at West2 47,269m3 5,000m3/day	22d	20-Apr-14 A	14-May-14 A					
East1 (North CH 225 - 325 & CH 5900 - 5800)									
A1665	PD - Earthwork Fill upto + 5.5 mPD at East1 47,269m3 10,000m3/day	7d	14-May-14 A	21-May-14	-207d				
East2 (North CH 325 - 450 & CH 5800 - 5700)									
A2170	PD - Earthwork Fill upto + 5.5 mPD at East2 47,268m3 10,000m3/day	7d	22-May-14	28-May-14	-207d				
Surcharge									
West1 Portion									
A1628	PD - Vent Shear Test after +5.5mPD 6nrs	12d	14-May-14 A	27-May-14	-126d				
A1638	PD - Allow to surcharge upto 8.5mPD by result of Vent Shear Test	0d		21-May-14	-125d				
A1640	PD - Surcharge Laying upto 8.5mPD at West1 42,843m3 5,000m3/day	15d	22-May-14	06-Jun-14	-144d				
A1650	PD - Surcharge compaction upto 8.5mPD at West1	15d	24-May-14	07-Jun-14	-160d				
A1652	PD - Vent Shear Test after +8.5mPD 6nrs	12d	09-Jun-14	21-Jun-14	-127d				
A1656	PD - Surcharge Pause Period at West1 0mths	0d	22-Jun-14	22-Jun-14	-159d				
A1658	PD - Surcharge Laying +11.5mPD at West1 42,843m3 5,000m3/day	8d	22-Jun-14	30-Jun-14	-143d				
A1660	PD - Surcharge Period at West1 4mths	120d	01-Jul-14	28-Oct-14	-159d				
West2 Portion									
A2192	PD - Vent Shear Test 6nrs	12d	28-May-14	11-Jun-14	-126d				
A2194	PD - Allow to surcharge upto 8.5mPD by result of Vent Shear Test	0d		11-Jun-14	-126d				

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Hong Kong Boundary Corssing Facilities - Reclamation Works

Data Date :21-May-14

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2014			
						May 30	Jun 31	Jul 32	Aug 33
A2200	PD - Surcharge Laying upto +8.5mPD at West2 42,843m3 5,000m3/day	9d	12-Jun-14	21-Jun-14	-143d				
A2210	PD - Surcharge compaction upto 8.5mPD at West2	9d	14-Jun-14	22-Jun-14	-150d				
A2212	PD - Vent Shear Test after +8.5mPD 6hrs	12d	23-Jun-14	07-Jul-14	-118d				
A2216	PD - Surcharge Pause Period at West2 0mths	0d	08-Jul-14	08-Jul-14	-147d				
A2218	PD - Surcharge Laying +11.5mPD at West2 42,843m3 5,000m3/day	8d	10-Jul-14	18-Jul-14	-138d				
A2220	PD - Surcharge Period at West2 4mths	120d	19-Jul-14	15-Nov-14	-149d				
East1 Portion		175d	12-Jun-14	03-Dec-14	-133d				
A1672	PD - Vent Shear Test 6hrs	12d	12-Jun-14	25-Jun-14	-118d				
A1673	PD - Allow to surcharge upto 8.5mPD by result of Vent Shear Test	0d		25-Jun-14	-118d				
A1675	PD - Surcharge Laying upto +8.5mPD at East1 42,843m3 5,000m3/day	9d	01-Jul-14	09-Jul-14	-138d				
A1680	PD - Surcharge Compaction upto 8.5mPD at East1	9d	02-Jul-14	10-Jul-14	-129d				
A1682	PD - Vent Shear Test after +8.5mPD 6hrs	12d	11-Jul-14	24-Jul-14	-103d				
A1686	PD - Surcharge Pause Period at East1 0mths	0d	25-Jul-14	25-Jul-14	-129d				
A1688	PD - Surcharge Laying +11.5mPD at East1 42,843m3 5,000m3/day	8d	29-Jul-14	05-Aug-14	-123d				
A1690	PD - Surcharge Period at East1 4mths	120d	06-Aug-14	03-Dec-14	-133d				
East2 Portion		56d	26-Jun-14	20-Aug-14	-121d				
A2234	PD - Vent Shear Test 6hrs	12d	26-Jun-14	10-Jul-14	-99d				
A2236	PD - Allow to surcharge upto 8.5 by result of Vent Shear Test	0d		10-Jul-14	-99d				
A2240	PD - Surcharge Laying upto +8.5mPD at East2 42843m3 5,000m3/day	9d	19-Jul-14	28-Jul-14	-123d				
A2250	PD - Surcharge Compaction upto 8.5mPD at East2	9d	21-Jul-14	29-Jul-14	-123d				
A2252	PD - Vent Shear Test after +8.5mPD 6hrs	12d	30-Jul-14	12-Aug-14	-97d				
A2256	PD - Surcharge Pause Period at East2 0mths	0d	13-Aug-14	13-Aug-14	-122d				
A2258	PD - Surcharge Laying +11.5mPD at East2 42,843m3 5,000m3/day	8d	13-Aug-14	20-Aug-14	-113d				
Box Curvert Construction		0d	19-Aug-14	19-Aug-14	-7d				
Extension Culvert EC1		0d	19-Aug-14	19-Aug-14	-7d				
EC1-0005	The Area of EC1 handback by HY/2011/03	0d	19-Aug-14*		-7d				◆

█ Remaining Level of Effort █ Remaining Work
█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone

Appendix C - Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
Air Quality				
S5.5.6.1 of HKBCFEIA	A1	The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	All construction sites	V
S5.5.6.2 of HKBCFEIA and S4.8.1 of TKCLKLEIA	A2	Proper watering of exposed spoil should be undertaken throughout the construction phase: <ul style="list-style-type: none"> • Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; • Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; • A stockpile of dusty material should not be extend beyond the pedestrian barriers, fencing or traffic cones. • Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores; • When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary 	All construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period;</p> <ul style="list-style-type: none"> • The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials; • Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously; • Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; • Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding; • Any skip hoist for material transport should be totally enclosed by impervious sheeting; • Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides; • Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an 		

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>audible high level alarm which is interlocked with the material filling line and no overfilling is allowed;</p> <ul style="list-style-type: none"> • All unpaved roads/exposed area shall be watered which results in dust suppression by forming moist cohesive films among the discrete grains of road surface material. • No burning of debris or other materials on the works areas is allowed; • Water spray shall be used during the handling of fill material at the site and at active cuts, excavation and fill sites where dust is likely to be created; • Open dropping heights for excavated materials shall be controlled to a maximum height of 2m to minimise the fugitive dust arising from unloading; • During transportation by truck, materials shall not be loaded to a level higher than the side and tail boards, and shall be dampened or covered before transport. Materials having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin. The tarpaulin shall be properly secured and shall extend at least 300mm over the edges of the side and tail boards; • Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system; and • Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable 		

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.		
S5.5.6.3 of HKBCFEIA and S4.8.1 of TKCLKLEIA	A3	The Contractor should undertake proper watering on all exposed spoil and associated work areas (with at least 8 times per day) throughout the construction phase.	All construction sites	V
S5.5.6.4 of HKBCFEIA and S4.11 of TKCLKLEIA	A4	Implement regular dust monitoring under EM&A programme during the construction stage.	Selected representative dust monitoring station	V
S5.5.7.1 of HKBCFEIA	A5	The following mitigation measures should be adopted to prevent fugitive dust emissions for concrete batching plant: <ul style="list-style-type: none"> • Loading, unloading, handling, transfer or storage of any dusty materials should be carried out in totally enclosed system; • All dust-laden air or waste gas generated by the process operations should be properly extracted and vented to fabric filtering system to meet the emission limits for TSP; • Vents for all silos and cement/ pulverised fuel ash (PFA) weighing scale should be fitted with fabric filtering system; • The materials which may generate airborne dusty emissions should be wetted by water spray system; 	All construction sites	N/A

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<ul style="list-style-type: none"> • All receiving hoppers should be enclosed on three sides up to 3m above unloading point; • All conveyor transfer points should be totally enclosed; • All access and route roads within the premises should be paved and wetted; and • Vehicle cleaning facilities should be provided and used by all concrete trucks before leaving the premises to wash off any dust on the wheels and/or body. 		
S5.5.2.7 of HKBCFEIA	A6	The following mitigation measures should be adopted to prevent fugitive dust emissions at barging point: <ul style="list-style-type: none"> • All road surface within the barging facilities will be paved; • Dust enclosures will be provided for the loading ramp; • Vehicles will be required to pass through designated wheels wash facilities; and • Continuous water spray at the loading points. 	All construction sites	N/A (Construction in process)
Construction Noise (Air borne)				
S6.4.10 of HKBCFEIA	N1	Use of good site practices to limit noise emissions by considering the following: <ul style="list-style-type: none"> • only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme; • machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; • plant known to emit noise strongly in one direction, where possible, be orientated 	All construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		so that the noise is directed away from nearby NSRs; <ul style="list-style-type: none"> • silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works; • mobile plant should be sited as far away from NSRs as possible and practicable; • material stockpiles, mobile container site office and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities. 		
S6.4.11 of HKBCFEIA	N2	Install temporary hoarding located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	All construction sites	V
S6.4.12 of HKBCFEIA	N3	Install movable noise barriers (typically density @14kg/m ²), acoustic mat or full enclosure close to noisy plants including air compressor, generators, saw.	For plant items listed in Appendix 6D of the EIA report at all construction sites	N/A
S6.4.13 of HKBCFEIA	N4	Select “Quiet plants” which comply with the BS 5228 Part 1 or TM standards.	For plant items listed in Appendix 6D of the EIA report at all construction sites	V
S6.4.14 of HKBCFEIA	N5	Sequencing operation of construction plants where practicable.	All construction sites where practicable	V
S5.1 of	N6	Implement a noise monitoring under EM&A programme.	Selected	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
TMCLKLEIA			representative noise monitoring station	
Waste Management (Construction Waste)				
S12.6 of TMCLKLEIA	WM1	The Contractor shall identify a coordinator for the management of waste.	All construction sites	V
S12.6 of TMCLKLEIA	WM2	The Contractor shall apply for and obtain the appropriate licenses for the disposal of public fill, chemical waste and effluent discharges.	All construction sites	V
S12.6 of TMCLKLEIA	WM3	EM&A of waste handling, storage, transportation, disposal procedures and documentation through the site audit programme shall be undertaken.	All construction sites	V
S8.3.8 of HKBCFEIA and S12.6 of TMCLKLEIA	WM4	<p><u>Construction and Demolition Material</u></p> <p>The following mitigation measures should be implemented in handling the waste:</p> <ul style="list-style-type: none"> • Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement; • Carry out on-site sorting; • Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; • Adopt ‘Selective Demolition’ technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible; 	All construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<ul style="list-style-type: none"> • Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified; • Implement an enhanced Waste Management Plan similar to ETWBTC (Works) No. 19/2005 – “Environmental Management on Construction Sites” to encourage on-site sorting of C&D materials and to minimize their generation during the course of construction; • In addition, disposal of the C&D materials onto any sensitive locations such as agricultural lands, etc. should be avoided. The Contractor shall propose the final disposal sites to the Project Proponent and get its approval before implementation; and • The surplus surcharge should be transferred to a fill bank. 		
S8.3.9- S8.3.11 of HKBCFEIA and S12.6 of TMCLKLEIA	WM5	<p><u>C&D Waste</u></p> <ul style="list-style-type: none"> • Standard formwork or pre-fabrication should be used as far as practicable in order to minimise the arising of C&D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding and falsework should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage. • The Contractor should recycle as much of the C&D materials as possible on-site. Public fill and C&D waste should be segregated and stored in different containers 	All construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>or skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and storage.</p>		
<p>S8.2.12- S8.3.15 of HKBCFEIA and S12.6 of TMCLKLEIA</p>	<p>WM6</p>	<p><u>Chemical Waste</u></p> <ul style="list-style-type: none"> • Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be handled in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. • Containers used for the storage of chemical wastes should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; have a capacity of less than 450 liters unless the specification has been approved by the EPD; and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the regulation. • The storage area for chemical wastes should be clearly labelled and used solely for the storage of chemical waste; enclosed on at least 3 sides; have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20 % of the total volume of waste stored in that area, whichever is the greatest; have adequate ventilation; covered to prevent rainfall entering; and arranged so that incompatible materials are adequately separated. • Disposal of chemical waste should be via a licensed waste collector; be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Centre 	<p>All construction sites</p>	<p>V</p>

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		which also offers a chemical waste collection service and can supply the necessary storage containers; or be to a reuser of the waste, under approval from the EPD.		
S8.3.16 of HKBCFEIA and S12.6 of TMCLKLEIA	WM7	<u>Sewage</u> <ul style="list-style-type: none"> • Adequate numbers of portable toilets should be provided for the workers. The portable toilets should be maintained in a state, which will not deter the workers from utilizing these portable toilets. Night soil should be collected by licensed collectors regularly. 	All construction sites	V
S8.3.17 of HKBCFEIA and S12.6 of TMCLKLEIA	WM8	<u>General Refuse</u> <ul style="list-style-type: none"> • The site and surroundings shall be kept tidy and litter free. General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes. • A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law. • Aluminium cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible. • Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be 	All construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>considered by the Contractor. In addition, waste separation facilities for paper, aluminum cans, plastic bottles etc., should be provided.</p> <ul style="list-style-type: none"> • Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including reduction, reuse and recycling of wastes. • Sufficient dustbins shall be provided for storage of waste as required under the Public Cleansing and Prevention of Nuisances By-laws. In addition, general refuse shall be cleared daily and shall be disposed of to the nearest licensed landfill or refuse transfer station. • All waste containers shall be in a secure area on hardstanding. 		
Water Quality (Construction Phase)				
	W1	<p>Mitigation during the marine works to reduce impacts to within acceptable levels have been recommended and will comprise a series of measures that restrict the method and sequencing of backfilling, as well as protection measures. Details of the measures are provided below:</p>	During filling	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<ul style="list-style-type: none"> • Reclamation filling for the Project shall not proceed until at least 200m of leading seawall at the reclamation area formed above +2.2mPD, unless otherwise agreement was obtained from EPD, except for the 300m gaps for marine access. All underwater filling works shall be carried out behind seawalls to avoid dispersion of suspended solids outside the Project limit; • Except for the filling of the cellular structures, not more than 15% public fill shall be used for reclamation filling below +2.5mPD during construction of the seawall; • After the seawall is completed except for the 300m marine access as indicated in the EPs, not more than 30% public fill shall be used for reclamation filling below +2.5mPD, unless otherwise agreement from EPD was obtained; • Upon completion of 200m leading seawall, no more than a total of 60 filling barge trips per day shall be made with a cumulative maximum daily filling rate of 60,000 m³ for HKBCF and TMCLKL southern landfall reclamation during the filling operation; and • Upon completion of the whole section of seawall except for the 300m marine access as indicated in the EPs, no more than a total of 190 filling barge trips per day shall be made with a cumulative maximum daily filling rate of 190,000 m³ for the remaining filling operations for HKBCF and TMCLKL southern landfall reclamation. • Floating type perimeter silt curtains shall be around the HKBCF site before the commencement of marine works. Staggered layers of silt curtain shall be provided 		

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>to prevent sediment loss at navigation accesses. The length of each staggered layers shall be at least 200m;</p> <ul style="list-style-type: none"> • Single layer silt curtain to be applied around the North-east airport water intake; • The silt-curtains should be maintained in good condition to ensure the sediment plume generated from filling be confined effectively within the site boundary; • The filling works shall be scheduled to spread the works evenly over a working day; • Cellular structure shall be used for seawall construction; • A layer of geotextile shall be placed on top of the seabed before any filling activities take place inside the cellular structures to form the seawall; • The conveyor belts shall be fitted with windboards and conveyor release points shall be covered with curtain to prevent any spillage of filling materials onto the surrounding waters; and • An additional layer of silt curtain shall be installed near the active stone column installation points. A layer of geotextile with stone blanket on top shall be placed on the seabed prior to stone column installation works. 		
S9.11.1.3 of HKBCFEIA and S6.10 of	W2	<p><u>Land Works</u></p> <p>General construction activities on land should also be governed by standard good working practice. Specific measures to be written into the works contracts should include:</p>	All land-based construction sites	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
TMCLKLEIA		<ul style="list-style-type: none"> • wastewater from temporary site facilities should be controlled to prevent direct discharge to surface or marine waters; • sewage effluent and discharges from on-site kitchen facilities shall be directed to Government sewer in accordance with the requirements of the WPCO or collected for disposal offsite. The use of soakaways shall be avoided; • storm drainage shall be directed to storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels, earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks; • silt removal facilities, channels and manholes shall be maintained and any deposited silt and grit shall be removed regularly, including specifically at the onset of and after each rainstorm; • temporary access roads should be surfaced with crushed stone or gravel; • rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities; • measures should be taken to prevent the washout of construction materials, soil, silt or debris into any drainage system; • open stockpiles of construction materials (e.g. aggregates and sand) on site 		

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<p>should be covered with tarpaulin or similar fabric during rainstorms;</p> <ul style="list-style-type: none"> • manholes (including any newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers; • discharges of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system; • all vehicles and plant should be cleaned before they leave the construction site to ensure that no earth, mud or debris is deposited by them on roads. A wheel washing bay should be provided at every site exit; • wheel wash overflow shall be directed to silt removal facilities before being discharged to the storm drain; • the section of construction road between the wheel washing bay and the public road should be surfaced with crushed stone or coarse gravel; • wastewater generated from concreting, plastering, internal decoration, cleaning work and other similar activities, shall be screened to remove large objects; • vehicle and plant servicing areas, vehicle wash bays and lubrication facilities shall be located under roofed areas. The drainage in these covered areas shall be connected to foul sewers via a petrol interceptor in accordance with the requirements of the WPCO or collected for offsite disposal; 		

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<ul style="list-style-type: none"> • the contractors shall prepare an oil / chemical cleanup plan and ensure that leakages or spillages are contained and cleaned up immediately; • waste oil should be collected and stored for recycling or disposal, in accordance with the Waste Disposal Ordinance; • all fuel tanks and chemical storage areas should be provided with locks and be sited on sealed areas. The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank; and • surface run-off from bunded areas should pass through oil/grease traps prior to discharge to the storm water system.. 		
S9.14 of HKBCFEIA and S6.10 of TMCLKLEIA	W3	Implement a water quality monitoring programme	At identified monitoring location	V
S6.10 of TMCLKLEIA	W4	All construction works shall be subject to routine audit to ensure implementation of all EIA recommendations and good working practice.	All construction site areas	V
Ecology (Construction Phase)				
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E1	<ul style="list-style-type: none"> • Install silt curtain during the construction • Limit works fronts • Construct seawall prior to reclamation filling where practicable 	Seawall, reclamation area	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		<ul style="list-style-type: none"> • Good site practices • Strict enforcement of no marine dumping • Site runoff control • Spill response plan 		
S10.7 of HKBCFEIA	E2	<ul style="list-style-type: none"> • Watering to reduce dust generation; prevention of siltation of freshwater habitats; Site runoff should be desilted, to reduce the potential for suspended sediments, organics and other contaminants to enter streams and standing freshwater. 	Land-based works areas	V
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E3	<ul style="list-style-type: none"> • Good site practices, including strictly following the permitted works hours, using quieter machines where practicable, and avoiding excessive lightings during night time. 	Land-based works areas	V
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E4	<ul style="list-style-type: none"> • Dolphin Exclusion Zone • Dolphin watching plan 	Marine works	V
S10.7 of HKBCFEIA and S8.14 of TMCLKLEIA	E5	<ul style="list-style-type: none"> • Decouple compressors and other equipment on working vessels • Proposal on design and implementation of acoustic decoupling measures applied during reclamation works • Avoidance of percussive piling 	Marine works	V
S10.7 of	E6	<ul style="list-style-type: none"> • Control vessel speed 	Marine traffic	V

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
HKBCFEIA and S8.14 of TMCLKLEIA		<ul style="list-style-type: none"> • Skipper training • Predefined and regular routes for working vessels; avoid Brothers Islands 		
S10.10 of HKBCFEIA and S8.14 of TMCLKLEIA	E7	<ul style="list-style-type: none"> • Vessel based dolphin monitoring 	Northeast and Northwest Lantau	V
Fisheries				
S11.7 of HKBCFEIA	F1	<ul style="list-style-type: none"> • Reduce re-suspension of sediments • Limit works fronts • Good site practices • Strict enforcement of no marine dumping • Spill response plan 	Seawall, reclamation area	V
S11.7 of HKBCFEIA	F2	<ul style="list-style-type: none"> • Install silt-grease trap in the drainage system collecting surface runoff 	Reclamation area	V
Landscape & Visual (Construction Phase)				
S14.3.3. 3 of HKBCFEIA and S10.9 of TMCLKLEIA	LV1	<p><u>Mitigate Landscape Impacts</u></p> <p>G1/CM4 Grass-hydroseed or sheeting bare soil surface and stock pile areas.</p> <p>G9 Reserve of loose natural granite rocks for re-use. Provide new coastline to adopt “natural-look” by means of using armour rocks in the form of natural</p>	All construction site areas	N/A

EIA Ref.	EM&A Log Ref	Environmental Mitigation Measures	Location	Implementation Status
		rock materials and planting strip area accommodating screen buffer to enhance “natural-look” of new coastline.		
S10.9 of TMCLKLEIA	LV2	<u>Mitigate Landscape Impacts</u> CM7 Ensure no run-off into water body adjacent to the Project Area.	All construction site areas	V
S14.3.3. 3 of HKBCFEIA	LV4	<u>Mitigate Visual Impacts</u> V1 Minimize time for construction activities during construction period.	All construction site areas	V
S10.9 of TMCLKLEIA	LV5	<u>Mitigate Visual Impacts</u> CM6 Control night-time lighting and glare by hooding all lights.	All construction site areas	V
EM&A				
S15.2.2 of HKBCFEIA	EM1	An Independent Environmental Checker needs to be employed as per the EM&A Manual.	All construction site areas	V
S15.5 - S15.6 of HKBCFEIA	EM2	<ul style="list-style-type: none"> An Environmental Team needs to be employed as per the EM&A Manual. Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures. An environmental impact monitoring needs to be implementing by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with. 	All construction site areas	V

Legend: V = implemented;

x = not implemented;

N/A = not applicable

Appendix D - Summary of Action and Limit Levels

Table 1 – Action and Limit Levels for 1-hour TSP

Location	Action Level	Limit Level
AMS2	374 $\mu\text{g}/\text{m}^3$	500 $\mu\text{g}/\text{m}^3$
AMS3A*	368 $\mu\text{g}/\text{m}^3$	500 $\mu\text{g}/\text{m}^3$
AMS6	360 $\mu\text{g}/\text{m}^3$	500 $\mu\text{g}/\text{m}^3$
AMS7	370 $\mu\text{g}/\text{m}^3$	500 $\mu\text{g}/\text{m}^3$

Remarks: * Action Level set out at AMS3 Ho Yu College is adopted.

Table 2 – Action and Limit Levels for 24-hour TSP

Location	Action Level	Limit Level
AMS2	176 $\mu\text{g}/\text{m}^3$	260 $\mu\text{g}/\text{m}^3$
AMS3A*	167 $\mu\text{g}/\text{m}^3$	260 $\mu\text{g}/\text{m}^3$
AMS6	173 $\mu\text{g}/\text{m}^3$	260 $\mu\text{g}/\text{m}^3$
AMS7	183 $\mu\text{g}/\text{m}^3$	260 $\mu\text{g}/\text{m}^3$

Remarks: * Action Level set out at AMS3 Ho Yu College is adopted.

Table 3 – Action and Limit Levels for Construction Noise (0700-1900 hrs of normal weekdays)

Location	Action Level	Limit Level
NMS2	When one documented complaint, related to 0700 – 1900 hours on normal weekdays, is received from any one of the sensitive receivers	75 dB(A)
NMS3A		*65 / 70 dB(A)

*Daytime noise Limit Level of 70 dB(A) applies to education institutions, while 65dB(A) applies during school examination period.

Table 4 – Action and Limit Levels for Water Quality

Parameters	Action	Limit
DO in mg L ⁻¹ (Surface, Middle & Bottom)	<u>Surface and Middle</u> 5.0 <u>Bottom</u> 4.7	<u>Surface and Middle</u> 4.2 (except 5 mg/L for FCZ) <u>Bottom</u> 3.6
SS in mg L ⁻¹ (depth-averaged)	23.5 and 120% of upstream control station's SS at the same tide of the same day	34.4 and 130% of upstream control station's SS at the same tide of the same day and 10mg/L for WSD Seawater intakes
Turbidity in NTU (depth-averaged)	27.5 and 120% of upstream control station's turbidity at the same tide of the same day	47.0 and 130% of upstream control station's turbidity at the same tide of the same day

Notes:

1. "depth-averaged" is calculated by taking the arithmetic means of reading of all three depths.
2. For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
3. For turbidity, SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

Table 5(a) Action and Limit Levels for Chinese White Dolphin Monitoring - Approach to Define Action Level (AL) and Limit Level (LL):

	North Lantau Social Cluster	
	NEL	NWL
Action Level	(STG < 70% of baseline) & (ANI < 70% of baseline)	(STG < 70% of baseline) & (ANI < 70% of baseline)
Limit Level	[(STG < 40% of baseline) & (ANI < 40% of baseline)] AND [(STG < 40% of baseline) & (ANI < 40% of baseline)]	

For North Lantau Social Cluster, action level will be trigger if either NEL **or** NWL fall below the criteria; limit level will be triggered if both NEL **and** NWL fall below the criteria.

Table 5(b) Derived Value of Action Level (AL) and Limit Level (LL) for Chinese White Dolphin Monitoring

	North Lantau Social Cluster	
	NEL	NWL
Action Level	(STG < 4.2) & (ANI < 15.5)	(STG < 6.9) & (ANI < 31.3)
Limit Level	[(STG < 2.4) & (ANI <8.9)] AND [(STG < 3.9)& (ANI < 17.9)]	

AECOM Asia Company Limited

TSP High Volume Sampler

Field Calibration Report

Station: Tung Chung Development Pier (AMS2) Operator: Cheung Hung Wai
 Cal. Date: 9-Apr-14 Next Due Date: 9-Jun-14
 Equipment No.: A-001-78T Serial No.: 3383

Ambient Condition			
Temperature, Ta (K)	293	Pressure, Pa (mmHg)	761.0

Orifice Transfer Standard Information					
Serial No:	988	Slope, mc	1.94727	Intercept, bc	0.02332
Last Calibration Date:	20-May-13	$mc \times Qstd + bc = [DH \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	20-May-14	$Qstd = \{[DH \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Resistance Plate No.	Orifice			HVS Flow Recorder	
	DH (orifice), in. of water	[DH x (Pa/760) x (298/Ta)] ^{1/2}	Qstd (m ³ /min) X-axis	Flow Recorder Reading (CFM)	Continuous Flow Recorder Reading IC (CFM) Y-axis
18	9.3	3.08	1.57	48.0	48.44
13	7.3	2.73	1.39	42.0	42.38
10	5.7	2.41	1.23	36.0	36.33
7	4.4	2.12	1.08	32.0	32.29
5	2.6	1.63	0.82	26.0	26.24

By Linear Regression of Y on X
 Slope, mw = 30.0178 Intercept, bw = 0.6308
 Correlation Coefficient* = 0.9904
 *If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 1.30m³/min
 From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = IC \times [(Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; IC = (mw x Qstd + bw) x [(760 / Pa) x (Ta / 298)]^{1/2} = 39.29

Remarks: _____

QC Reviewer:  Signature:  Date: 11 Apr 14

AECOM Asia Company Limited

TSP High Volume Sampler

Field Calibration Report

Station: Site Boundary of Site Office (WA2) (AMS3B) Operator: Leung Yiu Ting
 Cal. Date: 2-Apr-14 Next Due Date: 2-Jun-14
 Equipment No.: A-001-79T Serial No. 3384

Ambient Condition			
Temperature, Ta (K)	297	Pressure, Pa (mmHg)	763.2

Orifice Transfer Standard Information					
Serial No:	988	Slope, mc	1.94727	Intercept, bc	0.02332
Last Calibration Date:	20-May-13	$mc \times Qstd + bc = [DH \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	20-May-14	$Qstd = \{[DH \times (Pa/760) \times (298/Ta)]^{1/2} - bc\} / mc$			

Calibration of TSP Sampler					
Resistance Plate No.	Orifice			HVS Flow Recorder	
	DH (orifice), in. of water	[DH x (Pa/760) x (298/Ta)] ^{1/2}	Qstd (m ³ /min) X-axis	Flow Recorder Reading (CFM)	Continuous Flow Recorder Reading IC (CFM) Y-axis
18	8.3	2.89	1.47	48.0	48.21
13	6.8	2.62	1.33	43.0	43.18
10	5.2	2.29	1.16	34.0	34.15
7	4.1	2.03	1.03	28.0	28.12
5	2.5	1.59	0.80	19.0	19.08

By Linear Regression of Y on X

Slope, mw = 44.5628 Intercept, bw = -17.2050

Correlation Coefficient* = 0.9963

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation



From the TSP Field Calibration Curve, take Qstd = 1.30m³/min

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = IC \times [(Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; IC = (mw x Qstd + bw) x [(760 / Pa) x (Ta / 298)]^{1/2} = 40.55

Remarks: _____

QC Reviewer:  Signature:  Date: 3-Apr-14

AECOM Asia Company Limited

TSP High Volume Sampler

Field Calibration Report

Station: Hong Kong SkyCity Marriott Hotel (AMS7) Operator: Cheung Hung Wai
 Cal. Date: 9-Apr-14 Next Due Date: 9-Jun-14
 Equipment No.: A-001-80T Serial No.: 3385

Ambient Condition			
Temperature, Ta (K)	293	Pressure, Pa (mmHg)	761.0

Orifice Transfer Standard Information					
Serial No:	988	Slope, mc	1.94727	Intercept, bc	0.02332
Last Calibration Date:	20-May-13	$mc \times Qstd + bc = [DH \times (Pa/760) \times (298/Ta)]^{1/2}$			
Next Calibration Date:	20-May-14	$Qstd = \{ [DH \times (Pa/760) \times (298/Ta)]^{1/2} - bc \} / mc$			

Calibration of TSP Sampler					
Resistance Plate No.	Orifice			HVS Flow Recorder	
	DH (orifice), in. of water	[DH x (Pa/760) x (298/Ta)] ^{1/2}	Qstd (m ³ /min) X-axis	Flow Recorder Reading (CFM)	Continuous Flow Recorder Reading IC (CFM) Y-axis
18	7.8	2.82	1.44	46.0	46.42
13	6.6	2.59	1.32	40.0	40.37
10	5.2	2.30	1.17	32.0	32.29
7	4.1	2.04	1.04	26.0	26.24
5	3.0	1.75	0.89	20.0	20.18

By Linear Regression of Y on X

Slope, mw = 48.1386 Intercept, bw = -23.1991

Correlation Coefficient* = 0.9960

*If Correlation Coefficient < 0.990, check and recalibrate.

Set Point Calculation

From the TSP Field Calibration Curve, take Qstd = 1.30m³/min

From the Regression Equation, the "Y" value according to

$$mw \times Qstd + bw = IC \times [(Pa/760) \times (298/Ta)]^{1/2}$$

Therefore, Set Point; IC = (mw x Qstd + bw) x [(760 / Pa) x (Ta / 298)]^{1/2} = 39.02

Remarks: _____

QC Reviewer: Yun Fung

Signature: [Signature]

Date: 11 April 14



TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE
 VILLAGE OF CLEVELS, OH
 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - May 28, 2014 Rootsmeter S/N 0438320 Ta (K) - 296
 Operator Tisch Orifice I.D. - 0988 Pa (mm) - 751.84

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.3790	3.2	2.00
2	NA	NA	1.00	0.9720	6.4	4.00
3	NA	NA	1.00	0.8690	7.9	5.00
4	NA	NA	1.00	0.8260	8.8	5.50
5	NA	NA	1.00	0.6830	12.8	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9917	0.7191	1.4113	0.9957	0.7221	0.8874
0.9875	1.0159	1.9959	0.9915	1.0201	1.2549
0.9854	1.1339	2.2315	0.9894	1.1385	1.4030
0.9843	1.1916	2.3405	0.9883	1.1965	1.4715
0.9790	1.4333	2.8227	0.9829	1.4392	1.7747
Qstd slope (m) = 1.97518			Qa slope (m) = 1.23683		
intercept (b) = -0.01001			intercept (b) = -0.00630		
coefficient (r) = 0.99998			coefficient (r) = 0.99998		
y axis = $\text{SQRT}[\text{H2O}(\text{Pa}/760)(298/\text{Ta})]$			y axis = $\text{SQRT}[\text{H2O}(\text{Ta}/\text{Pa})]$		

CALCULATIONS

$V_{std} = \text{Diff. Vol}[(\text{Pa} - \text{Diff. Hg})/760](298/\text{Ta})$
 $Q_{std} = V_{std}/\text{Time}$

$V_a = \text{Diff Vol}[(\text{Pa} - \text{Diff Hg})/\text{Pa}]$
 $Q_a = V_a/\text{Time}$

For subsequent flow rate calculations:

$Q_{std} = 1/m\{[\text{SQRT}(\text{H2O}(\text{Pa}/760)(298/\text{Ta}))] - b\}$
 $Q_a = 1/m\{[\text{SQRT}(\text{H2O}(\text{Ta}/\text{Pa}))] - b\}$

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.07a
 Sensitivity Adjustment Scale Setting: 557 CPM
 Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 18 May 2013

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result


Sensitivity Adjustment Scale Setting (Before Calibration): 557 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 557 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	18-05-13	12:30 - 13:30	28.1	78	0.04714	1887	31.45
2	18-05-13	13:30 - 14:30	28.1	78	0.04932	1970	32.83
3	18-05-13	14:30 - 15:30	28.2	77	0.05156	2056	34.27
4	18-05-13	15:30 - 16:30	28.1	78	0.05083	2026	33.77

- Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X
 Slope (K-factor): 0.0015
 Correlation coefficient: 0.9978
 Validity of Calibration Record: 17 May 2014

Remarks:

QC Reviewer: YW Fung Signature:  Date: 20 May 2013

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.07a
 Sensitivity Adjustment Scale Setting: 557 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 10 May 2014

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 557 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 557 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	11-05-14	09:30 - 10:30	26.7	75	0.04434	1775	29.58
2	11-05-14	10:30 - 11:30	26.7	75	0.04716	1880	31.33
3	11-05-14	11:30 - 12:30	26.8	76	0.04927	1964	32.73
4	11-05-14	12:30 - 13:30	26.8	75	0.05035	2015	33.58

Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9982

Validity of Calibration Record: 11 May 2015

Remarks:

QC Reviewer: YW Fung

Signature: 

Date: 12 May 2014

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.08a
 Sensitivity Adjustment Scale Setting: 702 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 18 May 2013

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 702 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 702 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	18-05-13	12:30 - 13:30	28.1	78	0.04714	1764	29.40
2	18-05-13	13:30 - 14:30	28.1	78	0.04932	1846	30.77
3	18-05-13	14:30 - 15:30	28.2	77	0.05156	1935	32.25
4	18-05-13	15:30 - 16:30	28.1	78	0.05083	1899	31.65

- Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0016
 Correlation coefficient: 0.9976

Validity of Calibration Record: 17 May 2014

Remarks:

QC Reviewer: YW Fung Signature:  Date: 20 May 2013

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.08a
 Sensitivity Adjustment Scale Setting: 702 CPM
 Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K_o: 12500
 Last Calibration Date*: 10 May 2014

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 702 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 702 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	11-05-14	09:45 - 10:45	26.7	75	0.04568	1713	28.50
2	11-05-14	10:45 - 11:45	26.7	75	0.04857	1819	30.32
3	11-05-14	11:45 - 12:45	26.8	76	0.05063	1903	31.72
4	11-05-14	12:45 - 13:45	26.8	75	0.05116	1922	32.03


- Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0016
 Correlation coefficient: 0.9984

Validity of Calibration Record: 11 May 2015

Remarks:

QC Reviewer: YW Fung Signature:  Date: 12 May 2014

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.09a
 Sensitivity Adjustment Scale Setting: 797 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 18 May 2013

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 797 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 797 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	18-05-13	12:30 - 13:30	28.1	78	0.04714	1885	31.42
2	18-05-13	13:30 - 14:30	28.1	78	0.04932	1965	32.75
3	18-05-13	14:30 - 15:30	28.2	77	0.05156	2059	34.32
4	18-05-13	15:30 - 16:30	28.1	78	0.05083	2024	33.73

Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9973

Validity of Calibration Record: 17 May 2014

Remarks:

QC Reviewer: YW Fung Signature:  Date: 20 May 2013

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.09a
 Sensitivity Adjustment Scale Setting: 797 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 10 May 2014

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 797 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 797 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	11-05-14	13:30 - 14:30	26.8	75	0.05034	2017	33.62
2	11-05-14	14:30 - 15:30	26.9	76	0.05211	2084	34.73
3	11-05-14	15:30 - 16:30	26.9	76	0.05163	2066	34.43
4	11-05-14	16:30 - 17:30	26.9	76	0.05272	2113	35.22

Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9965

Validity of Calibration Record: 11 May 2015

Remarks:

QC Reviewer: YW Fung

Signature: 

Date: 12 May 2014

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.10a
 Sensitivity Adjustment Scale Setting: 753 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 18 May 2013

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 753 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 753 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	18-05-13	12:30 - 13:30	28.1	78	0.04714	1886	31.43
2	18-05-13	13:30 - 14:30	28.1	78	0.04932	1968	32.80
3	18-05-13	14:30 - 15:30	28.2	77	0.05156	2061	34.35
4	18-05-13	15:30 - 16:30	28.1	78	0.05083	2026	33.77

- Note:
1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9983

Validity of Calibration Record: 17 May 2014

Remarks:

QC Reviewer: YW Fung

Signature: 

Date: 20 May 2013

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.10a
 Sensitivity Adjustment Scale Setting: 753 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K_o: 12500
 Last Calibration Date*: 10 May 2014

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 753 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 753 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	11-05-14	13:45 - 14:45	26.8	75	0.04984	1996	33.27
2	11-05-14	14:45 - 15:45	26.9	76	0.05196	2077	34.62
3	11-05-14	15:45 - 16:45	26.9	76	0.05141	2055	34.25
4	11-05-14	16:45 - 17:45	26.9	76	0.05263	2109	35.15

- Note:
1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9969

Validity of Calibration Record: 11 May 2015

Remarks:

QC Reviewer: YW Fung Signature:  Date: 12 May 2014

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.11a
 Sensitivity Adjustment Scale Setting: 799 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 18 May 2013

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 799 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 799 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	18-05-13	12:15 - 13:15	28.1	78	0.04685	1871	31.18
2	18-05-13	13:15 - 14:15	28.1	78	0.04941	1979	32.98
3	18-05-13	14:15 - 15:15	28.2	77	0.05127	2055	34.25
4	18-05-13	15:15 - 16:15	28.1	78	0.05060	2021	33.68

- Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9976

Validity of Calibration Record: 17 May 2014

Remarks:

QC Reviewer: YW Fung Signature:  Date: 20 May 2013

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3
 Equipment No.: A.005.11a
 Sensitivity Adjustment Scale Setting: 799 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K_o: 12500
 Last Calibration Date*: 10 May 2014

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 799 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 799 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	18-05-14	09:00 - 10:00	28.3	77	0.04527	1815	30.25
2	18-05-14	10:00 - 11:00	28.3	77	0.04811	1923	32.05
3	18-05-14	11:00 - 12:00	28.3	77	0.05103	2041	34.02
4	18-05-14	12:00 - 13:00	28.4	77	0.05366	2157	35.95

Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9987

Validity of Calibration Record: 18 May 2015

Remarks:

QC Reviewer: YW Fung Signature:  Date: 19 May 2014

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3B
 Equipment No.: A.005.13a
 Sensitivity Adjustment Scale Setting: 643 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 18 May 2013

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 643 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 643 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	18-05-13	12:15 - 13:15	28.1	78	0.04685	1867	31.12
2	18-05-13	13:15 - 14:15	28.1	78	0.04941	1975	32.92
3	18-05-13	14:15 - 15:15	28.2	77	0.05127	2048	34.13
4	18-05-13	15:15 - 16:15	28.1	78	0.05060	2017	33.62

Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9986

Validity of Calibration Record: 17 May 2014

Remarks:

QC Reviewer: YW Fung Signature:  Date: 20 May 2013

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3B
 Equipment No.: A.005.13a
 Sensitivity Adjustment Scale Setting: 643 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K_o: 12500
 Last Calibration Date*: 10 May 2014

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 643 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 643 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	18-05-14	09:30 - 10:30	28.3	77	0.04614	1846	30.77
2	18-05-14	10:30 - 11:30	28.3	77	0.04823	1934	32.23
3	18-05-14	11:30 - 12:30	28.3	77	0.05152	2053	34.22
4	18-05-14	12:30 - 13:30	28.4	77	0.05391	2162	36.03

- Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0015
 Correlation coefficient: 0.9981

Validity of Calibration Record: 18 May 2015

Remarks:

QC Reviewer: YW Fung

Signature: 

Date: 19 May 2014

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3B
 Equipment No.: A.005.14a
 Sensitivity Adjustment Scale Setting: 786 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 18 May 2013

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 786 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 786 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	18-05-13	12:15 - 13:15	28.1	78	0.04685	2005	33.42
2	18-05-13	13:15 - 14:15	28.1	78	0.04941	2121	35.35
3	18-05-13	14:15 - 15:15	28.2	77	0.05127	2194	36.57
4	18-05-13	15:15 - 16:15	28.1	78	0.05060	2167	36.12

- Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0014
 Correlation coefficient: 0.9987

Validity of Calibration Record: 17 May 2014

Remarks:

QC Reviewer: YW Fung Signature:  Date: 20 May 2013

EQUIPMENT CALIBRATION RECORD

Type: Laser Dust Monitor
 Manufacturer/Brand: SIBATA
 Model No.: LD-3B
 Equipment No.: A.005.14a
 Sensitivity Adjustment Scale Setting: 786 CPM

Operator: Mike Shek (MSKM)

Standard Equipment

Equipment: Rupprecht & Patashnick TEOM®
 Venue: Cyberport (Pui Ying Secondary School)
 Model No.: Series 1400AB
 Serial No: Control: 140AB219899803
 Sensor: 1200C143659803 K₀: 12500
 Last Calibration Date*: 10 May 2014

*Remarks: Recommended interval for hardware calibration is 1 year

Calibration Result

Sensitivity Adjustment Scale Setting (Before Calibration): 786 CPM
 Sensitivity Adjustment Scale Setting (After Calibration): 786 CPM

Hour	Date (dd-mm-yy)	Time	Ambient Condition		Concentration ¹ (mg/m ³) Y-axis	Total Count ²	Count/ Minute ³ X-axis
			Temp (°C)	R.H. (%)			
1	18-05-14	12:45 - 13:45	28.4	77	0.05027	2158	35.97
2	18-05-14	13:45 - 14:45	28.5	76	0.05161	2211	36.85
3	18-05-14	14:45 - 15:45	28.5	76	0.05235	2247	37.45
4	18-05-14	15:45 - 16:45	28.4	77	0.05203	2233	37.22


Note: 1. Monitoring data was measured by Rupprecht & Patashnick TEOM®
 2. Total Count was logged by Laser Dust Monitor
 3. Count/minute was calculated by (Total Count/60)

By Linear Regression of Y or X

Slope (K-factor): 0.0014
 Correlation coefficient: 0.9969

Validity of Calibration Record: 18 May 2015

Remarks:

QC Reviewer: YW Fung Signature:  Date: 19 May 2014



CERTIFICATE OF CALIBRATION

Certificate No.: 13CA1107 01-02

Page: 1 of 2

Item tested

Description: Acoustical Calibrator (Class 1)
Manufacturer: Rion Co., Ltd.
Type/Model No.: NC-73
Serial/Equipment No.: 10307223 / N.004.08
Adaptors used: -

Item submitted by

Customer: AECOM ASIA CO., LTD.
Address of Customer: -
Request No.: -
Date of receipt: 07-Nov-2013

Date of test: 08-Nov-2013

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2341427	17-Apr-2014	SCL
Preamplifier	B&K 2673	2239857	16-Apr-2014	CEPREI
Measuring amplifier	B&K 2610	2346941	24-Apr-2014	CEPREI
Signal generator	DS 360	61227	15-Apr-2014	CEPREI
Digital multi-meter	34401A	US36087050	10-Dec-2013	CEPREI
Audio analyzer	8903B	GB41300350	15-Apr-2014	CEPREI
Universal counter	53132A	MY40003662	15-Apr-2014	CEPREI

Ambient conditions

Temperature: 22 ± 1 °C
Relative humidity: 60 ± 10 %
Air pressure: 1000 ± 10 hPa

Test specifications

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942: 1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.

Approved Signatory:

Huang Jian Min/Feng Jun Qi

Date: 11-Nov-2013

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



CERTIFICATE OF CALIBRATION

Certificate No.: 13CA1107 01-01 Page 1 of 2

Item tested

Description:	Sound Level Meter (Type 1)	, Microphone
Manufacturer:	Rion Co., Ltd.	, Rion Co., Ltd.
Type/Model No.:	NL-31	, UC-53A
Serial/Equipment No.:	00320528 / N.007.03A	, 90565
Adaptors used:	-	, -

Item submitted by

Customer Name: AECOM ASIA CO., LTD.
Address of Customer: -
Request No.: -
Date of receipt: 07-Nov-2013

Date of test: 08-Nov-2013

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Multi function sound calibrator	B&K 4226	2288444	22-Jun-2014	CIGISMEC
Signal generator	DS 360	33873	15-Apr-2014	CEPREI
Signal generator	DS 360	61227	15-Apr-2014	CEPREI

Ambient conditions

Temperature: 22 ± 1 °C
Relative humidity: 60 ± 10 %
Air pressure: 1000 ± 10 hPa

Test specifications

- 1, The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- 2, The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of $\pm 20\%$.
- 3, The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsiveness of the Sound Level Meter.


Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Approved Signatory:


Huang Jian Min/Feng Jun Qi

Date: 11-Nov-2013

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.



CERTIFICATE OF CALIBRATION

Certificate No.: 14CA0305 06-01 Page 1 of 2

Item tested

Description:	Sound Level Meter (Type 1)	Microphone
Manufacturer:	B & K	B & K
Type/Model No.:	2238	4188
Serial/Equipment No.:	2285692 <i>N.009.04</i>	2250420
Adaptors used:	-	-

Item submitted by

Customer Name: AECOM ASIA CO. LTD.
Address of Customer: -
Request No.: -
Date of receipt: 05-Mar-2014

Date of test: 07-Mar-2014

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Multi function sound calibrator	B&K 4226	2288444	22-Jun-2014	CIGISMEC
Signal generator	DS 360	33873	15-Apr-2014	CEPREI
Signal generator	DS 360	61227	15-Apr-2014	CEPREI

Ambient conditions

Temperature: 22 ± 1 °C
Relative humidity: 60 ± 10 %
Air pressure: 1000 ± 10 hPa

Test specifications

- 1, The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- 2, The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of $\pm 20\%$.
- 3, The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsiveness of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Approved Signatory:

Huang Jian Min/Feng Jun Qi

Date: 12-Mar-2014

Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Work Order: HK1404442
Date of Issue: 20/02/2014
Client: AECOM ASIA COMPANY LIMITED



Equipment Type: Sonde Environmental Monitoring System
Brand Name: YSI
Model No.: 6820 V2
Serial No.: 12D100972
Equipment No.: W.026.36
Date of Calibration: 13 February, 2014 **Date of next Calibration:** 13 May, 2014

Parameters:

Conductivity

Method Ref: APHA (21st edition), 2510B

Expected Reading (uS/cm)	Displayed Reading (uS/cm)	Tolerance (%)
146.9	150.5	2.5
6667	6566	-1.5
12890	12650	-1.9
58670	57730	-1.6
Tolerance Limit (±%)		10.0

Dissolved Oxygen

Method Ref: APHA (21st edition), 4500O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.40	3.35	-0.05
5.50	5.47	-0.03
7.65	7.62	-0.03
Tolerance Limit (±mg/L)		0.20

pH Value

Method Ref: APHA 21st Ed. 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	4.04	0.04
7.0	7.06	0.06
10.0	10.05	0.05
Tolerance Limit (±pH unit)		0.20

Salinity

Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.02	--
10	9.85	-1.5
20	19.78	-1.1
30	29.54	-1.5
Tolerance Limit (±%)		10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.


 Mr. Fung Lim Chee, Richard
 General Manager
 Greater China & Hong Kong

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order: HK1404442
Date of Issue: 20/02/2014
Client: AECOM ASIA COMPANY LIMITED



Equipment Type: Sonde Environmental Monitoring System
Brand Name: YSI
Model No.: 6820 V2
Serial No.: 12D100972
Equipment No.: W.026.36
Date of Calibration: 13 February, 2014 **Date of next Calibration:** 13 May, 2014

Parameters:

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
14.0	14.06	0.1
26.0	25.88	-0.1
38.5	38.45	0.0
	Tolerance Limit (±°C)	2.0

Turbidity

Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.0	--
4	4.0	0.0
10	10.3	3.0
20	20.4	2.0
50	50.5	1.0
100	100.7	0.7
	Tolerance Limit (±%)	10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Work Order: HK1414461
Date of Issue: 19/05/2014
Client: AECOM ASIA COMPANY LIMITED



Description: Sonde
Brand Name: YSI
Model No.: 6820 V2
Serial No.: 12D100972
Equipment No.: W.026.36
Date of Calibration: 13 May, 2014

Date of next Calibration: 13 August, 2014

Parameters:

Conductivity

Method Ref: APHA (20th edition), 2510B

Expected Reading (uS/cm)	Displayed Reading (uS/cm)	Tolerance (%)
146.9	145.8	-0.7
6667	6640	-0.4
12890	12750	-1.1
58670	58200	-0.8
Tolerance Limit (%)		±10.0

Dissolved Oxygen Method Ref: APHA (21st edition), 4500: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.66	3.69	+0.03
5.85	5.81	-0.04
7.65	7.60	-0.05
Tolerance Limit (mg/L)		±0.20

pH Value

Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	4.03	+0.03
7.0	7.05	+0.05
10.0	10.03	+0.03
Tolerance Limit (pH Unit)		±0.20

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

 Mr Fung Lim Chee, Richard
 General Manager
 Greater China & Hong Kong

REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Work Order: HK1414461
Date of Issue: 19/05/2014
Client: AECOM ASIA COMPANY LIMITED



Description: Sonde
Brand Name: YSI
Model No.: 6820 V2
Serial No.: 12D100972
Equipment No.: W.026.36
Date of Calibration: 13 May, 2014

Date of next Calibration: 13 August, 2014

Parameters:

Salinity

Method Ref: APHA (21st edition), 2520B

Expected Reading (g/L)	Displayed Reading (g/L)	Tolerance (%)
0	0.02	--
10	9.94	-0.6
20	19.56	-2.2
30	29.76	-0.8
Tolerance Limit (%)		±10.0

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Reading of Ref. thermometer (°C)	Displayed Reading (°C)	Tolerance (°C)
13.5	13.37	-0.1
25.5	25.53	+0.0
38.0	38.06	+0.1
Tolerance Limit (°C)		±2.0

Turbidity

Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.0	--
4	3.9	-2.5
10	9.8	-2.0
20	20.4	+2.0
50	50.5	+1.0
100	101.2	+1.2
Tolerance Limit (%)		±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.



 Mr Fung Lim Chee, Richard
 General Manager -
 Greater China & Hong Kong

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



Work Order: HK1404435
Date of Issue: 20/02/2014
Client: AECOM ASIA COMPANY LIMITED

Equipment Type: Sonde Environmental Monitoring System
Brand Name: YSI
Model No.: 6820 V2
Serial No.: 12A101545
Equipment No.: W.026.35
Date of Calibration: 13 February, 2014 **Date of next Calibration:** 13 May, 2014

Parameters:

Conductivity

Method Ref: APHA (21st edition), 2510B

Expected Reading (uS/cm)	Displayed Reading (uS/cm)	Tolerance (%)
146.9	151.0	2.8
6667	6558	-1.6
12890	12670	-1.7
58670	58020	-1.1
Tolerance Limit (±%)		10.0

Dissolved Oxygen

Method Ref: APHA (21st edition), 4500O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.40	3.42	0.02
5.50	5.54	0.04
7.65	7.60	-0.05
Tolerance Limit (±mg/L)		0.20

pH Value

Method Ref: APHA 21st Ed. 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	4.02	0.02
7.0	7.05	0.05
10.0	9.97	-0.03
Tolerance Limit (±pH unit)		0.20

Salinity

Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.03	--
10	9.88	-1.2
20	19.62	-1.9
30	29.50	-1.7
Tolerance Limit (±%)		10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr. Fung Lim Chee, Richard
 General Manager -
 Greater China & Hong Kong

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



Work Order: HK1404435
Date of Issue: 20/02/2014
Client: AECOM ASIA COMPANY LIMITED

Equipment Type: Sonde Environmental Monitoring System
Brand Name: YSI
Model No.: 6820 V2
Serial No.: 12A101545
Equipment No.: W.026.35
Date of Calibration: 13 February, 2014 **Date of next Calibration:** 13 May, 2014

Parameters:

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
14.0	13.92	-0.1
26.0	25.91	-0.1
38.5	38.40	-0.1
Tolerance Limit (±°C)		2.0

Turbidity

Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.0	--
4	3.9	-2.5
10	9.7	-3.0
20	19.6	-2.0
50	49.3	-1.4
100	99.2	-0.8
Tolerance Limit (±%)		10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Work Order: HK1414464
Date of Issue: 19/05/2014
Client: AECOM ASIA COMPANY LIMITED



Description: Sonde
Brand Name: YSI
Model No.: 6820 V2
Serial No.: 12A101545
Equipment No.: W.026.35
Date of Calibration: 13 May, 2014

Date of next Calibration: 13 August, 2014

Parameters:

Conductivity

Method Ref: APHA (20th edition), 2510B

Expected Reading (uS/cm)	Displayed Reading (uS/cm)	Tolerance (%)
146.9	147.2	+0.2
6667	6710	+0.6
12890	12710	-1.4
58670	58520	-0.3
Tolerance Limit (%)		±10.0

Dissolved Oxygen Method Ref: APHA (21st edition), 4500: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
3.66	3.70	+0.04
5.85	5.89	+0.04
7.65	7.70	+0.05
Tolerance Limit (mg/L)		±0.20

pH Value

Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	4.01	+0.01
7.0	7.05	+0.05
10.0	9.94	-0.06
Tolerance Limit (pH Unit)		±0.20

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.


 Mr Fung Lim Chee, Richard
 General Manager -
 Greater China & Hong Kong

REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Work Order: HK1414464
Date of Issue: 19/05/2014
Client: AECOM ASIA COMPANY LIMITED



Description: Sonde
Brand Name: YSI
Model No.: 6820 V2
Serial No.: 12A101545
Equipment No.: W.026.35
Date of Calibration: 13 May, 2014

Date of next Calibration: 13 August, 2014

Parameters:

Salinity

Method Ref: APHA (21st edition), 2520B

Expected Reading (g/L)	Displayed Reading (g/L)	Tolerance (%)
0	0.00	--
10	9.68	-3.2
20	19.86	-0.7
30	29.72	-0.9
Tolerance Limit (%)		±10.0

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Reading of Ref. thermometer (°C)	Displayed Reading (°C)	Tolerance (°C)
13.5	13.42	-0.1
25.5	24.40	-1.1
38.0	37.66	-0.3
Tolerance Limit (°C)		±2.0

Turbidity

Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.0	--
4	4.1	+2.5
10	10.0	0.0
20	19.8	-1.0
50	49.5	-1.0
100	99.6	-0.4
Tolerance Limit (%)		±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

 Mr Fung Lim Chee, Richard
 General Manager
 Greater China & Hong Kong

**Hong Kong Boundary Crossing Facilities – Reclamation Works
Impact Monitoring Schedule for May 2014**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1-May	2-May	3-May
					Mid-Flood 8:07 Mid-Ebb 15:00 24-hour TSP 1-hour TSP	
4-May	5-May	6-May	7-May	8-May	9-May	10-May
	Mid-Flood 9:38 Mid-Ebb 16:58		Mid-Flood 11:28 Mid-Ebb 18:48 24-hour TSP 1-hour TSP Noise	Dolphin Monitoring Dolphin Monitoring	Mid-Ebb 9:43 Mid-Flood 15:05 Dolphin Monitoring*	
11-May	12-May	13-May	14-May	15-May	16-May	17-May
	Mid-Ebb 11:30 Mid-Flood 17:53 Dolphin Monitoring 24-hour TSP 1-hour TSP Noise		Mid-Ebb 12:39 Mid-Flood 19:26		Mid-Flood 7:16 Mid-Ebb 13:57	24-hour TSP 1-hour TSP
18-May	19-May	20-May	21-May	22-May	23-May	24-May
	Mid-Flood 9:23 Mid-Ebb 16:19		Mid-Flood 11:34 Mid-Ebb 18:19		Mid-Ebb 9:09 Mid-Flood 14:37 24-hour TSP 1-hour TSP Noise	
25-May	26-May	27-May	28-May	29-May	30-May	31-May
	Mid-Ebb 11:32 Mid-Flood 17:56 Dolphin Monitoring**	Dolphin Monitoring	Mid-Ebb 12:48 Mid-Flood 19:40	24-hour TSP 1-hour TSP Noise	Mid-Flood 7:06 Mid-Ebb 14:03	Dolphin Monitoring

The schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather, etc)

*Boat survey on 9 May 14 was cancelled due to predicted adverse weather

**Boat survey on 26 May 14 was rescheduled to 31 May 14

**Hong Kong Boundary Crossing Facilities – Reclamation Works
Tentative Impact Monitoring Schedule for June 2014**

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1-Jun	2-Jun	3-Jun	4-Jun	5-Jun	6-Jun	7-Jun
	Mid-Flood 8:46 Mid-Ebb 15:51	Dolphin Monitoring	Mid-Flood 10:04 Mid-Ebb 17:07 24-hour TSP 1-hour TSP Noise	Dolphin Monitoring	Mid-Flood 12:31 Mid-Ebb 18:55	
8-Jun	9-Jun	10-Jun	11-Jun	12-Jun	13-Jun	14-Jun
	Mid-Ebb 10:18 Mid-Flood 16:44 24-hour TSP 1-hour TSP Noise		Mid-Ebb 11:38 Mid-Flood 18:31		Mid-Ebb 13:02 Mid-Flood 20:11	24-hour TSP 1-hour TSP
15-Jun	16-Jun	17-Jun	18-Jun	19-Jun	20-Jun	21-Jun
	Mid-Flood 8:28 Mid-Ebb 15:20 Dolphin Monitoring	Dolphin Monitoring	Mid-Flood 10:19 Mid-Ebb 17:02		Mid-Flood 12:56 Mid-Ebb 19:05 24-hour TSP 1-hour TSP Noise	
22-Jun	23-Jun	24-Jun	25-Jun	26-Jun	27-Jun	28-Jun
	Mid-Ebb 10:29 Mid-Flood 16:59		Mid-Ebb 11:54 Mid-Flood 18:51	24-hour TSP 1-hour TSP Noise	Mid-Ebb 13:10 Mid-Flood 20:10	
29-Jun	30-Jun					
	Mid-Flood 7:56 Mid-Ebb 14:55					

The schedule is subject to change due to unforeseeable circumstances (e.g. adverse weather, etc)

Appendix G Impact Air Quality Monitoring Results

1-hour TSP Monitoring Results at Station AMS2 - Tung Chung Development Pier

Date	Session	Weather Condition	averaged Wind Speed (m/s)*	Time (hh:mm)	Conc. ($\mu\text{g}/\text{m}^3$)	Actino Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
2-May-14	1st Hour	Sunny	0.5	10:08	81	374	500
2-May-14	2nd Hour	Sunny	3.1	11:08	82	374	500
2-May-14	3rd Hour	Sunny	2.1	12:08	83	374	500
7-May-14	1st Hour	Fine	2.50	10:28	83	374	500
7-May-14	2nd Hour	Fine	0.25	11:28	83	374	500
7-May-14	3rd Hour	Fine	0.08	12:28	83	374	500
12-May-14	1st Hour	Sunny	0.97	11:37	84	374	500
12-May-14	2nd Hour	Sunny	1.17	12:37	84	374	500
12-May-14	3rd Hour	Sunny	0.29	13:37	81	374	500
17-May-14	1st Hour	Sunny	3.58	10:15	74	374	500
17-May-14	2nd Hour	Sunny	0.46	11:15	73	374	500
17-May-14	3rd Hour	Sunny	1.52	12:15	75	374	500
23-May-14	1st Hour	Rainy	1.38	10:34	77	374	500
23-May-14	2nd Hour	Rainy	1.40	11:34	76	374	500
23-May-14	3rd Hour	Rainy	2.32	12:34	77	374	500
29-May-14	1st Hour	Sunny	2.81	10:13	84	374	500
29-May-14	2nd Hour	Sunny	4.43	11:13	84	374	500
29-May-14	3rd Hour	Sunny	4.59	12:13	83	374	500
					Average	80	
					Min	73	
					Max	84	

1-hour TSP Monitoring Results at Station AMS3B - Site Boundary of Site Office (WA2)

Date	Session	Weather Condition	averaged Wind Speed (m/s)*	Time (hh:mm)	Conc. ($\mu\text{g}/\text{m}^3$)	Actino Level ($\mu\text{g}/\text{m}^3$) ^	Limit Level ($\mu\text{g}/\text{m}^3$)
2-May-14	1st Hour	Sunny	0.5	10:22	84	368	500
2-May-14	2nd Hour	Sunny	3.1	11:22	82	368	500
2-May-14	3rd Hour	Sunny	2.1	12:22	84	368	500
7-May-14	1st Hour	Fine	2.50	10:37	82	368	500
7-May-14	2nd Hour	Fine	0.25	11:37	82	368	500
7-May-14	3rd Hour	Fine	0.08	12:37	84	368	500
12-May-14	1st Hour	Sunny	0.97	11:25	83	368	500
12-May-14	2nd Hour	Sunny	1.17	12:25	82	368	500
12-May-14	3rd Hour	Sunny	0.29	13:25	84	368	500
17-May-14	1st Hour	Sunny	3.58	10:25	72	368	500
17-May-14	2nd Hour	Sunny	0.46	11:25	71	1006	500
17-May-14	3rd Hour	Sunny	1.52	12:25	73	368	500
23-May-14	1st Hour	Rainy	1.38	10:45	77	368	500
23-May-14	2nd Hour	Rainy	1.40	11:45	77	368	500
23-May-14	3rd Hour	Rainy	2.32	12:45	78	368	500
29-May-14	1st Hour	Sunny	2.81	11:45	84	368	500
29-May-14	2nd Hour	Sunny	4.43	12:45	82	368	500
29-May-14	3rd Hour	Sunny	4.59	13:45	83	368	500
					Average	80	
					Min	71	
					Max	84	

Remarks:

^ Action Level set out at AMS3 Ho Yu College is adopted.

1-hour TSP Monitoring Results at Station AMS7 - Hong Kong SkyCity Marriott Hotel

Date	Session	Weather Condition	averaged Wind Speed (m/s)*	Time (hh:mm)	Conc. ($\mu\text{g}/\text{m}^3$)	Actino Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
2-May-14	1st Hour	Sunny	0.5	10:38	83	370	500
2-May-14	2nd Hour	Sunny	3.1	11:38	82	370	500
2-May-14	3rd Hour	Sunny	2.1	12:38	84	370	500
7-May-14	1st Hour	Fine	2.50	10:12	84	370	500
7-May-14	2nd Hour	Fine	0.25	11:12	81	370	500
7-May-14	3rd Hour	Fine	0.08	12:12	83	370	500
12-May-14	1st Hour	Sunny	0.97	11:49	84	370	500
12-May-14	2nd Hour	Sunny	1.17	12:49	82	370	500
12-May-14	3rd Hour	Sunny	0.29	13:49	82	370	500
17-May-14	1st Hour	Sunny	3.58	10:00	78	370	500
17-May-14	2nd Hour	Sunny	0.46	11:00	75	370	500
17-May-14	3rd Hour	Sunny	1.52	12:00	76	370	500
23-May-14	1st Hour	Rainy	1.38	10:20	76	370	500
23-May-14	2nd Hour	Rainy	1.40	11:20	75	370	500
23-May-14	3rd Hour	Rainy	2.32	12:20	76	370	500
29-May-14	1st Hour	Sunny	2.81	10:00	83	370	500
29-May-14	2nd Hour	Sunny	4.43	11:00	83	370	500
29-May-14	3rd Hour	Sunny	4.59	12:00	81	370	500
					Average	80	
					Min	75	
					Max	84	

Appendix G Impact Air Quality Monitoring Results

24-hour TSP Monitoring Results at Station AMS2 - Tung Chung Development Pier

Start Date	Start Time	End Date	End Time	Weather Condition	Air Temp. (°C)	Atmospheric Pressure(hPa)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Filter Weight (g)		Particulate weight(g)	Elapse Time		Sampling Time(hrs.)	Conc. (µg/m ³)	Actino Level (µg/m ³)	Limit Level (µg/m ³)
							Initial	Final			Initial	Final		Initial	Final				
2-May-14	9:00	3-May-14	9:00	Sunny	24.0	1015.0	1.33	1.33	1.33	1912.3	2.7149	2.7930	0.0781	3341.84	3365.84	24.00	41	176	260
7-May-14	9:00	8-May-14	9:00	Fine	20.4	1013.6	1.33	1.33	1.33	1513.9	2.6993	2.7637	0.0644	3365.84	3384.84	19.00	43	176	260
12-May-14	9:00	13-May-14	9:00	Cloudy	25.8	1008.5	1.33	1.33	1.33	1912.3	2.7684	2.8597	0.0913	3389.84	3413.84	24.00	48	176	260
16-May-14	16:00	17-May-14	16:00	Sunny	28.3	1008.8	1.33	1.33	1.33	1912.3	2.7610	2.7955	0.0345	3413.84	3437.84	24.00	18	176	260
22-May-14	16:00	23-May-14	16:00	Rainy	29.1	1005.7	1.33	1.33	1.33	1912.3	2.7750	2.8243	0.0493	3437.84	3461.84	24.00	26	176	260
28-May-14	16:00	29-May-14	16:00	Sunny	29.4	1007.4	1.33	1.33	1.33	1912.3	2.6797	2.7138	0.0341	3461.84	3485.84	24.00	18	176	260
																Average	32		
																Min	18		
																Max	48		

24-hour TSP Monitoring Results at Station AMS3B - Site Boundary of Site Office (WA2)

Start Date	Start Time	End Date	End Time	Weather Condition	Air Temp. (°C)	Atmospheric Pressure(hPa)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Filter Weight (g)		Particulate weight(g)	Elapse Time		Sampling Time(hrs.)	Conc. (µg/m ³)	Actino Level (µg/m ³)	Limit Level (µg/m ³)
							Initial	Final			Initial	Final		Initial	Final				
2-May-14	9:00	3-May-14	9:00	Sunny	24.0	1015.0	1.33	1.33	1.33	1917.1	2.7145	2.8785	0.1640	3277.80	3301.86	24.06	86	167	260
7-May-14	9:00	8-May-14	9:00	Fine	20.4	1013.6	1.33	1.33	1.33	1912.3	2.7237	2.7894	0.0657	3301.80	3325.80	24.00	34	167	260
12-May-14	9:00	13-May-14	9:00	Cloudy	25.8	1008.5	1.33	1.33	1.33	1912.3	2.7577	2.8397	0.0820	3325.80	3349.80	24.00	43	167	260
16-May-14	16:00	17-May-14	16:00	Sunny	28.3	1008.8	1.33	1.33	1.33	1912.3	2.7401	2.7807	0.0406	3349.80	3373.80	24.00	21	167	260
22-May-14	16:00	23-May-14	16:00	Rainy	29.1	1005.7	1.33	1.33	1.33	1912.3	2.7604	2.8121	0.0517	3373.80	3397.80	24.00	27	167	260
28-May-14	16:00	29-May-14	16:00	Sunny	29.4	1007.4	1.33	1.33	1.33	1916.6	2.6543	2.6846	0.0303	3397.80	3421.80	24.00	16	167	260
																Average	38		
																Min	16		
																Max	86		




Remarks:

^ Action Level set out at AMS3 Ho Yu College is adopted.

24-hour TSP Monitoring Results at Station AMS7 - Hong Kong SkyCity Marriott Hotel

Start Date	Start Time	End Date	End Time	Weather Condition	Air Temp. (°C)	Atmospheric Pressure(hPa)	Flow Rate (m ³ /min.)		Av. flow (m ³ /min)	Total vol. (m ³)	Filter Weight (g)		Particulate weight(g)	Elapse Time		Sampling Time(hrs.)	Conc. (µg/m ³)	Actino Level (µg/m ³)	Limit Level (µg/m ³)
							Initial	Final			Initial	Final		Initial	Final				
2-May-14	9:00	3-May-14	9:00	Sunny	24.0	1015.0	1.33	1.33	1.33	1916.6	2.7223	2.8233	0.1010	3299.98	3323.98	24.00	53	183	260
7-May-14	9:00	8-May-14	9:00	Fine	20.4	1013.6	1.34	1.34	1.34	1925.3	2.7312	2.8108	0.0796	3323.98	3347.98	24.00	41	183	260
12-May-14	9:00	13-May-14	9:00	Cloudy	25.8	1008.5	1.34	1.34	1.34	1925.3	2.7651	2.8794	0.1143	3347.98	3371.98	24.00	59	183	260
16-May-14	16:00	17-May-14	16:00	Sunny	28.3	1008.8	1.34	1.34	1.34	1925.3	2.7285	2.7677	0.0392	3371.98	3395.98	24.00	20	183	260
22-May-14	16:00	23-May-14	16:00	Rainy	29.1	1005.7	1.34	1.34	1.34	1925.3	2.7885	2.8426	0.0541	3395.98	3419.98	24.00	28	183	260
28-May-14	16:00	29-May-14	16:00	Sunny	29.4	1007.4	1.34	1.34	1.34	1925.3	2.6345	2.7585	0.1240	3419.98	3443.98	24.00	64	183	260
																Average	43		
																Min	20		
																Max	64		

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

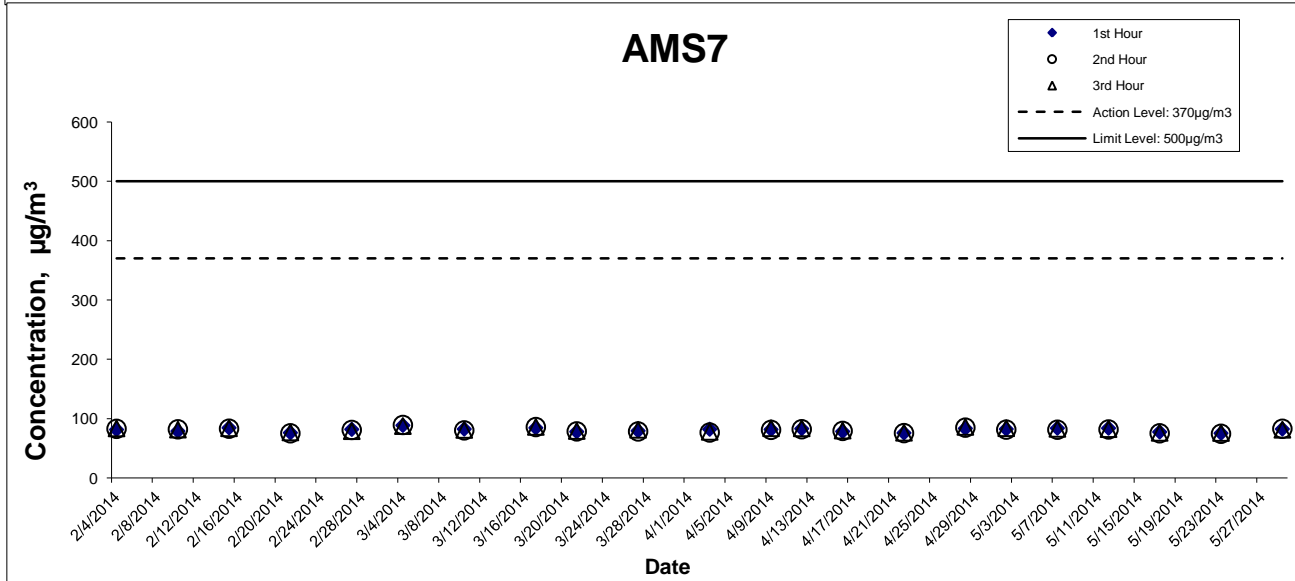
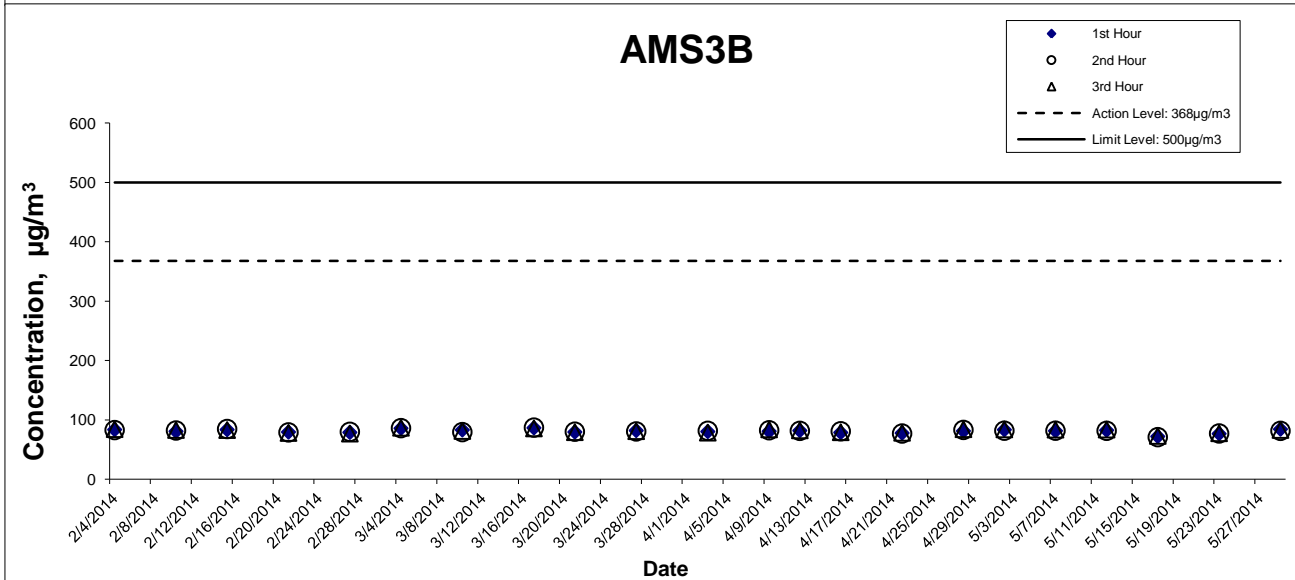
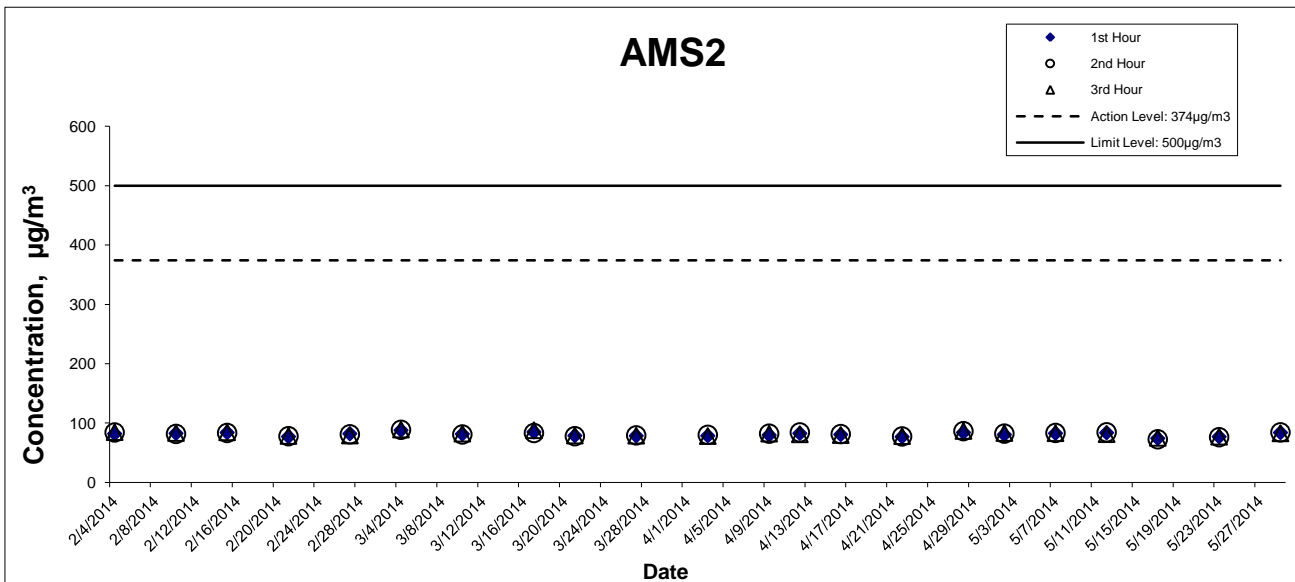


This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

**Graphical Presentation of Impact 1-hour TSP
 Monitoring Results**



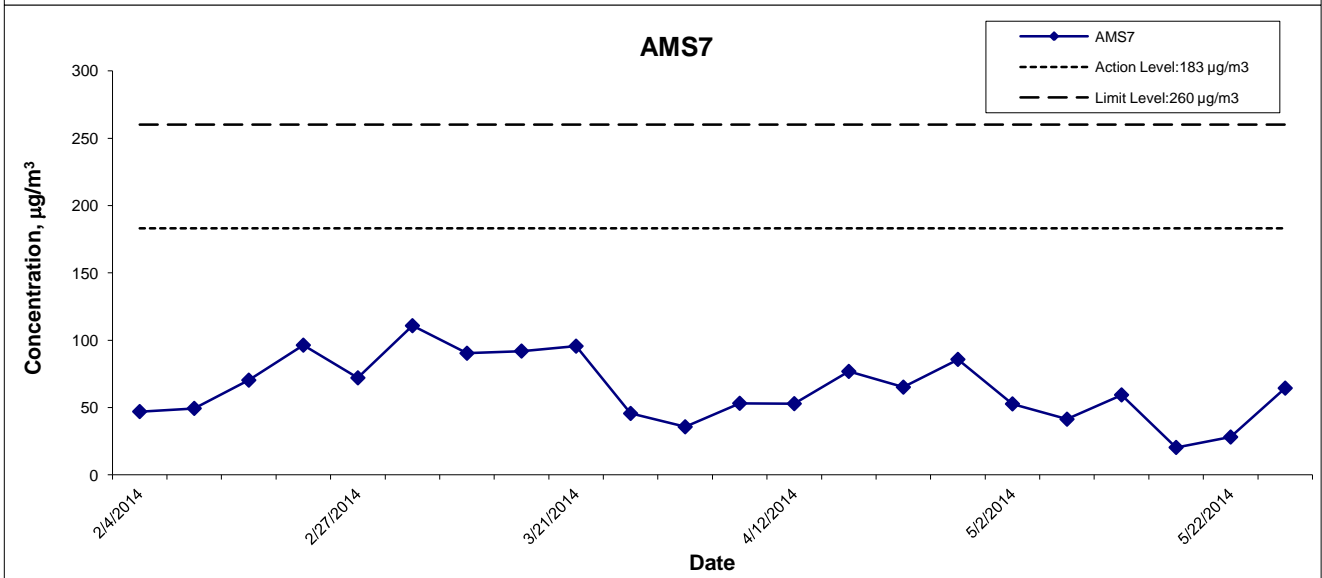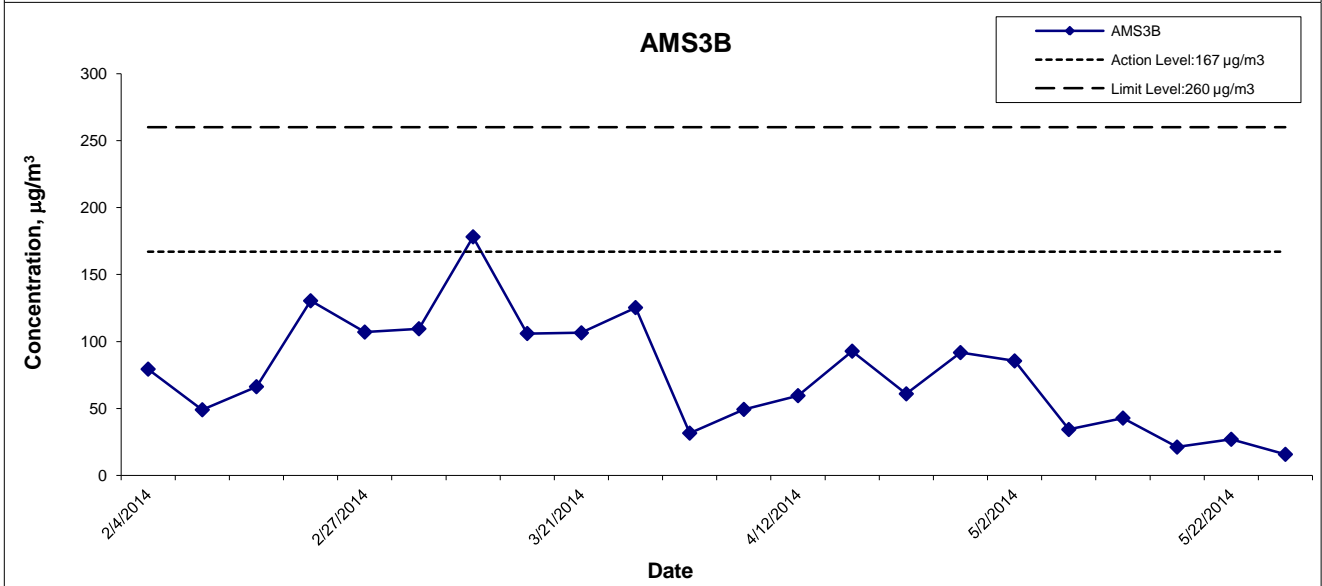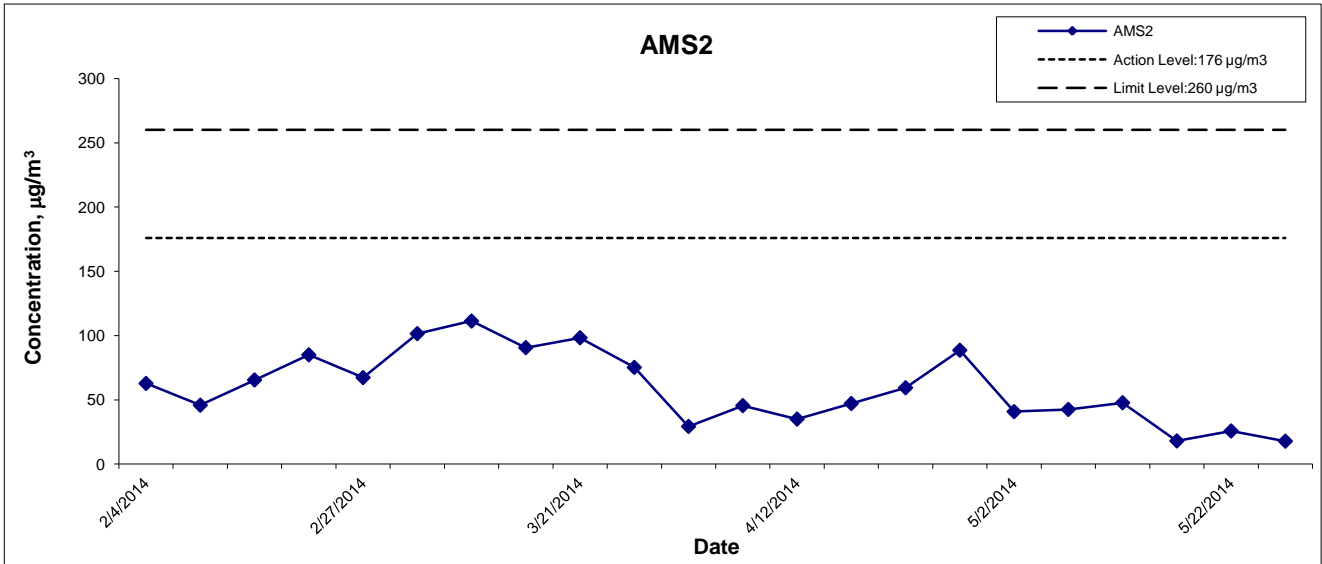

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

APPENDIX H Meteorological Data for Monitoring Periods on Monitoring Dates in May 2014

WIND DATA

Date	Time	Averaged Wind Speed (m/s)	Averaged Wind Direction (degrees)
05/02/14	09:18:24	1.94	108
05/02/14	10:18:24	0.46	286
05/02/14	11:18:24	3.06	128
05/02/14	12:18:24	2.07	136
05/02/14	13:18:24	0.41	58
05/02/14	14:18:24	0.04	72
05/02/14	15:18:24	0.14	342
05/02/14	16:18:24	1.64	69
05/02/14	17:18:24	0.24	250
05/02/14	18:18:24	0.27	173
05/02/14	19:18:24	0.04	86
05/02/14	20:18:24	2.17	112
05/02/14	21:18:24	0.06	156
05/02/14	22:18:24	2.91	132
05/02/14	23:18:24	3.73	140
05/03/14	00:18:24	3.33	150
05/03/14	01:18:24	3.90	90
05/03/14	02:18:24	2.04	101
05/03/14	03:18:24	0.91	145
05/03/14	04:18:24	0.99	140
05/03/14	05:18:24	1.48	133
05/03/14	06:18:24	0.15	174
05/03/14	07:18:24	0.69	103
05/03/14	08:18:24	0.55	109
05/03/14	09:18:24	2.91	136
05/07/14	09:18:24	1.62	155
05/07/14	10:18:24	2.50	145
05/07/14	11:18:24	0.25	129
05/07/14	12:18:24	0.08	162
05/07/14	13:18:24	0.03	78
05/07/14	14:18:24	0.03	63
05/07/14	15:18:24	0.43	122
05/07/14	16:18:24	0.74	131
05/07/14	17:18:24	1.50	167
05/07/14	18:18:24	0.69	128
05/07/14	19:18:24	5.30	130
05/07/14	20:18:24	3.57	128
05/07/14	21:18:24	2.04	171
05/07/14	22:18:24	3.64	138
05/07/14	23:18:24	2.29	171
05/08/14	00:18:24	3.94	152
05/08/14	01:18:24	0.42	127
05/08/14	02:18:24	2.21	125
05/08/14	03:18:24	0.08	171
05/08/14	04:18:24	0.03	135
05/08/14	05:18:24	0.46	118
05/08/14	06:18:24	0.35	126
05/08/14	07:18:24	0.55	111
05/08/14	08:18:24	0.46	70
05/08/14	09:18:24	0.11	137
05/12/14	09:18:24	0.49	330
05/12/14	10:18:24	1.08	144
05/12/14	11:18:24	0.97	135
05/12/14	12:18:24	1.17	138
05/12/14	13:18:24	0.29	113
05/12/14	14:18:24	0.67	128
05/12/14	15:18:24	0.28	126
05/12/14	16:18:24	0.41	112
05/12/14	17:18:24	0.53	117
05/12/14	18:18:24	0.88	336
05/12/14	19:18:24	0.76	336
05/12/14	20:18:24	0.80	359
05/12/14	21:18:24	0.80	140
05/12/14	22:18:24	0.87	66
05/12/14	23:18:24	0.78	144
05/13/14	00:18:24	0.92	123
05/13/14	01:18:24	1.58	117
05/13/14	02:18:24	1.19	115
05/13/14	03:18:24	1.44	182
05/13/14	04:18:24	1.37	142
05/13/14	05:18:24	1.27	118
05/13/14	06:18:24	1.97	130
05/13/14	07:18:24	1.83	147
05/13/14	08:18:24	1.31	346
05/13/14	09:18:24	1.37	299
05/16/14	16:18:24	1.12	41
05/16/14	17:18:24	1.34	117
05/16/14	18:18:24	1.71	293
05/16/14	19:18:24	1.87	346
05/16/14	20:18:24	1.23	35
05/16/14	21:18:24	1.13	168
05/16/14	22:18:24	1.52	160
05/16/14	23:18:24	1.33	103
05/17/14	00:18:24	1.96	151
05/17/14	01:18:24	1.20	69
05/17/14	02:18:24	1.29	76
05/17/14	03:18:24	0.80	340
05/17/14	04:18:24	1.78	186
05/17/14	05:18:24	1.30	57

APPENDIX H Meteorological Data for Monitoring Periods on Monitoring Dates in May 2014

WIND DATA

Date	Time	Averaged Wind Speed (m/s)	Averaged Wind Direction (degrees)
05/17/14	06:18:24	0.64	141
05/17/14	07:18:24	0.60	146
05/17/14	08:18:24	0.84	53
05/17/14	09:18:24	2.57	62
05/17/14	10:18:24	3.58	312
05/17/14	11:18:24	0.46	313
05/17/14	12:18:24	1.52	57
05/17/14	13:18:24	0.81	313
05/17/14	14:18:24	0.70	336
05/17/14	15:18:24	1.96	199
05/17/14	16:18:24	1.33	349
05/17/14	17:18:24	2.87	327
05/22/14	16:18:24	1.45	342
05/22/14	17:18:24	1.54	65
05/22/14	18:18:24	1.76	74
05/22/14	19:18:24	1.57	41
05/22/14	20:18:24	2.14	78
05/22/14	21:18:24	1.58	293
05/22/14	22:18:24	1.54	11
05/22/14	23:18:24	2.07	59
05/23/14	00:18:24	1.62	316
05/23/14	01:18:24	1.99	121
05/23/14	02:18:24	1.78	95
05/23/14	03:18:24	3.76	253
05/23/14	04:18:24	3.09	355
05/23/14	05:18:24	1.93	295
05/23/14	06:18:24	1.51	355
05/23/14	07:18:24	2.15	305
05/23/14	08:18:24	1.44	318
05/23/14	09:18:24	2.77	277
05/23/14	10:18:24	1.38	27
05/23/14	11:18:24	1.40	31
05/23/14	12:18:24	2.32	317
05/23/14	13:18:24	0.85	339
05/23/14	14:18:24	0.88	280
05/23/14	15:18:24	0.80	277
05/23/14	16:18:24	0.83	84
05/28/14	16:18:24	1.71	7
05/28/14	17:18:24	1.24	322
05/28/14	18:18:24	1.26	244
05/28/14	19:18:24	2.57	314
05/28/14	20:18:24	1.43	158
05/28/14	21:18:24	0.24	96
05/28/14	22:18:24	0.52	279
05/28/14	23:18:24	0.15	116
05/29/14	00:18:24	0.39	86
05/29/14	01:18:24	0.22	51
05/29/14	02:18:24	0.21	309
05/29/14	03:18:24	0.18	146
05/29/14	04:18:24	0.18	113
05/29/14	05:18:24	0.18	116
05/29/14	06:18:24	0.27	218
05/29/14	07:18:24	0.52	120
05/29/14	08:18:24	0.28	136
05/29/14	09:18:24	1.22	314
05/29/14	10:18:24	2.81	333
05/29/14	11:18:24	4.43	331
05/29/14	12:18:24	4.59	332
05/29/14	13:18:24	5.72	340
05/29/14	14:18:24	3.38	320
05/29/14	15:18:24	4.03	339
05/29/14	16:18:24	1.89	311

Appendix I Impact Daytime Construction Noise Monitoring Results

Daytime Noise Monitoring Results at Station NMS2 - Seaview Crescent Tower 1

Date	Weather Condition	Noise Level for 30-min, dB(A) [#]				Averaged Wind Speed (m/s)	Baseline Noise Level, dB(A)	Limit Level, dB(A)	Exceedance (Y/N)
		Time	L90	L10	Leq				
7-May-14	Fine	10:46	63	69	67	<5m/s	62.9	75	N
12-May-14	Sunny	10:30	63	69	66	<5m/s	62.9	75	N
23-May-14	Cloudy	15:42	59	67	65	<5m/s	62.9	75	N
29-May-14	Sunny	12:00	62	68	65	<5m/s	62.9	75	N
		Min	62	66	65				
		Max	64	71	67				
		Average	--	--	66				

Daytime Noise Monitoring Results at Station NMS3B - Site Boundary of Site Office (WA2)

Date	Weather Condition	Noise Level for 30-min, dB(A) [#]				Averaged Wind Speed (m/s)	Baseline Noise Level, dB(A) ^	Limit Level, dB(A)**	Exceedance (Y/N)
		Time	L90	L10	Leq ^{>}				
7-May-14	Fine	11:30	62	68	66	<5m/s	66.3	70	N
12-May-14	Sunny	11:15	61	67	65	<5m/s	66.3	70	N
23-May-14	Cloudy	14:28	60	63	62	<5m/s	66.3	70	N
29-May-14	Sunny	10:50	63	65	66	<5m/s	66.3	70	N
		Min	58	67	64				
		Max	63	71	70				
		Average	--	--	65				



Remark:

[#] A correction of +3dB(A) was made to the free field measurement.

* Façade measurement.

^ Averaged baseline noise level recorded at NMS3 Ho Yu College is adopted.

** Limit Level of 70dB(A) applies to education institutes while 65dB(A) applies during school examination period.

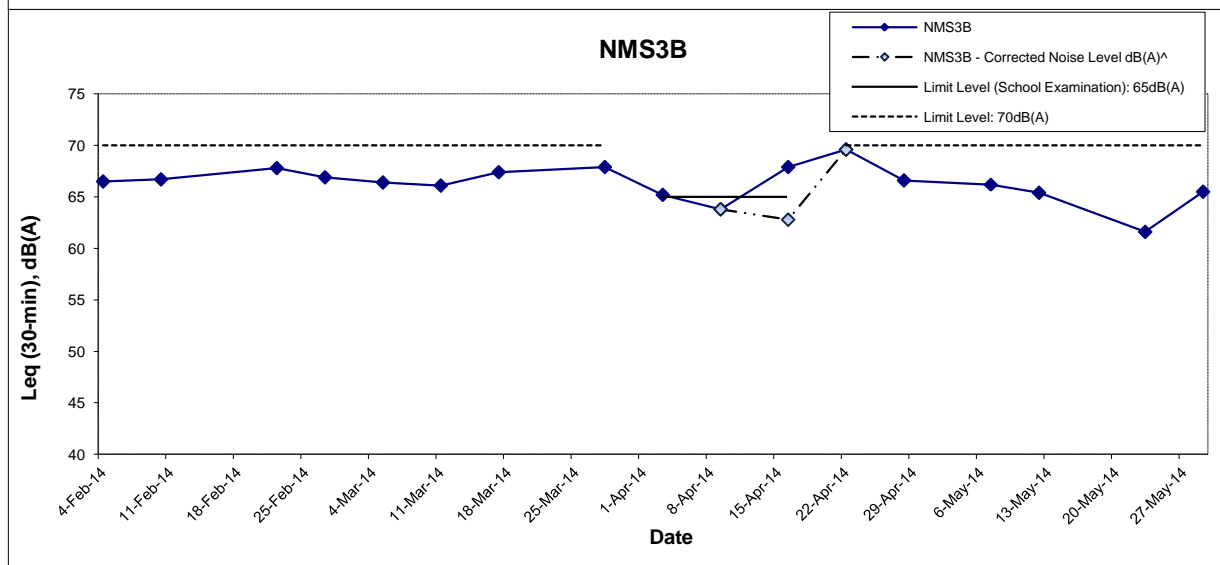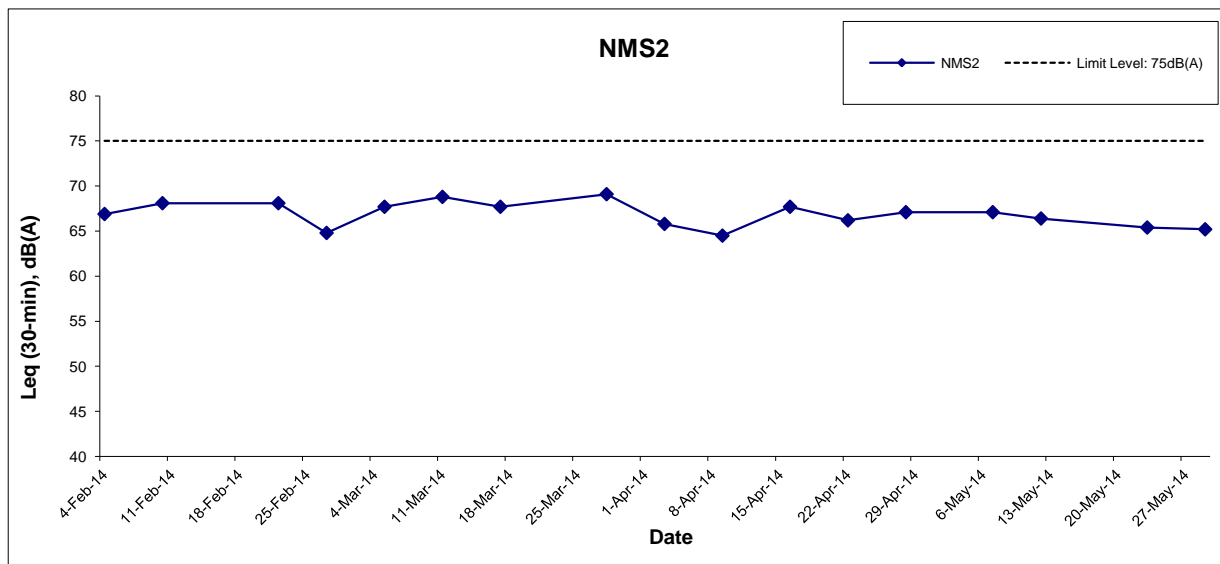

Remarks: Effective from July 2012, the Limit Level at NMS3A was revised to 70dB(A). Daytime noise Limit Level of 70 dB(A) applies to education institutions, while 65dB(A) applies during school examination period.

^The measured noise level on 16 April 2014 exceeded the noise level of 65dB(A) during examination period on 16 April 2014 but it is lower than the baseline level. Therefore, baseline correction was carried out and the corrected noise level which solely represent the noise level of Construction works is 63 dB(A) which is lower than the exceedance level of 65dB(A). As such the EAP was not triggered.

This Drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)3 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	14:39	6.5	Surface	1.0	24.5 24.5	24.5	8.2 8.2	8.2	26.7 26.7	26.7	91.7 91.7	91.7	6.6 6.6	6.6	6.6	4.6 4.8	4.7	5.2	5.3 5.1	5.2	4.8
					Middle	3.3	24.3 24.3	24.3	8.2 8.2	8.2	26.8 27.1	26.9	91.7 91.8	91.8	6.6 6.6	6.6		5.5 5.3	5.4		3.8 5.5	4.7	
					Bottom	5.5	24.0 24.1	24.0	8.2 8.2	8.2	29.1 29.4	29.3	90.9 90.7	90.8	6.5 6.5	6.5		5.4 5.4	5.4		5.2 4.0	4.6	
5-May-14	Sunny	Moderate	16:39	6.2	Surface	1.0	24.3 24.3	24.3	8.3 8.3	8.3	24.8 24.8	24.8	91.3 91.3	91.3	6.6 6.6	6.6	6.6	2.2 2.1	2.2	2.3	4.0 3.3	3.7	4.7
					Middle	3.1	24.3 24.3	24.3	8.3 8.3	8.3	26.7 26.7	26.7	91.0 91.1	91.1	6.6 6.6	6.6		2.1 2.2	2.2		5.2 5.7	5.5	
					Bottom	5.2	24.2 24.3	24.2	8.3 8.2	8.3	28.7 28.4	28.5	91.7 91.5	91.6	6.5 6.5	6.5		2.5 2.5	2.5		5.5 4.5	5.0	
7-May-14	Cloudy	Moderate	18:26	6.3	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	28.0 28.1	28.0	90.8 91.3	91.1	6.6 6.6	6.6	6.6	2.3 2.3	2.3	2.5	6.7 6.5	6.6	6.2
					Middle	3.2	23.6 23.6	23.6	8.2 8.2	8.2	29.3 29.1	29.2	90.2 91.0	90.6	6.5 6.5	6.5		2.6 2.5	2.6		5.2 6.9	6.1	
					Bottom	5.3	23.6 23.6	23.6	8.2 8.2	8.2	29.7 29.4	29.5	90.0 90.9	90.5	6.4 6.5	6.5		2.5 2.6	2.6		6.6 5.4	6.0	
9-May-14	Rainy	Moderate	10:15	6.3	Surface	1.0	23.6 23.6	23.6	8.1 8.2	8.2	27.3 27.2	27.3	88.1 87.7	87.9	6.4 6.4	6.4	6.3	8.9 9.2	9.1	11.3	4.8 6.2	5.5	5.7
					Middle	3.2	23.7 23.7	23.7	8.2 8.1	8.1	30.4 30.4	30.4	86.6 87.5	87.1	6.2 6.2	6.2		10.8 11.2	11.0		5.4 5.2	5.3	
					Bottom	5.3	23.7 23.7	23.7	8.2 8.1	8.1	30.5 30.5	30.5	87.2 88.9	88.1	6.2 6.3	6.3		14.0 13.8	13.9		6.6 5.9	6.3	
12-May-14	Sunny	Moderate	11:55	6.4	Surface	1.0	24.2 24.2	24.2	7.9 7.8	7.8	14.4 12.8	13.6	82.6 84.2	83.4	6.4 6.6	6.5	6.5	3.7 3.6	3.7	3.8	5.0 4.3	4.7	5.7
					Middle	3.2	23.9 23.9	23.9	7.6 7.9	7.7	16.1 16.2	16.1	84.4 82.2	83.3	6.5 6.3	6.4		3.6 3.7	3.7		6.2 6.7	6.5	
					Bottom	5.4	23.9 23.9	23.9	7.8 7.4	7.6	16.8 18.0	17.4	82.6 86.0	84.3	6.3 6.5	6.4		4.0 3.7	3.9		6.5 5.5	6.0	
14-May-14	Sunny	Moderate	13:08	6.5	Surface	1.0	25.2 25.1	25.1	8.1 8.1	8.1	17.5 17.5	17.5	82.8 85.1	84.0	6.2 6.4	6.3	6.3	6.3 6.6	6.5	9.8	6.8 6.6	6.7	6.5
					Middle	3.3	24.6 24.6	24.6	8.1 8.1	8.1	20.5 18.9	19.7	81.2 85.4	83.3	6.0 6.4	6.2		9.3 9.6	9.5		6.7 5.1	5.9	
					Bottom	5.5	24.6 24.6	24.6	8.1 8.1	8.1	22.4 22.2	22.3	88.1 83.3	85.7	6.5 6.1	6.3		13.1 13.9	13.5		5.9 7.6	6.8	
16-May-14	Cloudy	Moderate	13:25	6.9	Surface	1.0	25.4 25.5	25.5	8.1 8.1	8.1	17.7 17.5	17.6	82.1 82.3	82.2	6.1 6.1	6.1	6.1	9.6 9.7	9.7	10.0	6.2 4.7	5.5	6.1
					Middle	3.5	25.2 25.2	25.2	8.1 8.1	8.1	20.8 20.5	20.6	81.6 81.6	81.6	6.0 6.0	6.0		10.0 9.9	10.0		7.0 6.1	6.6	
					Bottom	5.9	25.2 25.2	25.2	8.0 8.0	8.0	21.9 21.3	21.6	81.8 81.7	81.8	5.9 6.0	6.0		10.4 10.2	10.3		5.8 6.5	6.2	
19-May-14	Sunny	Rough	16:32	7.1	Surface	1.0	26.9 26.9	26.9	8.1 8.1	8.1	14.2 14.1	14.2	84.3 84.4	84.4	6.2 6.2	6.2	6.2	4.2 4.0	4.1	4.3	4.6 5.0	4.8	5.0
					Middle	3.6	26.1 26.1	26.1	8.1 8.1	8.1	16.5 16.1	16.3	81.8 83.0	82.4	6.0 6.1	6.1		4.3 4.5	4.4		4.3 4.9	4.6	
					Bottom	6.1	26.0 25.8	25.9	8.1 8.0	8.0	18.3 19.4	18.8	81.5 82.1	81.8	6.0 6.1	6.0		4.4 4.5	4.5		5.0 5.9	5.5	
21-May-14	Cloudy	Moderate	17:50	6.5	Surface	1.0	26.0 26.6	26.3	8.1 8.1	8.1	13.5 12.8	13.2	70.7 76.3	73.5	5.3 5.7	5.5	5.4	3.8 3.6	3.7	5.7	5.7 6.2	6.0	6.5
					Middle	3.3	26.0 25.9	25.9	8.1 8.0	8.1	17.7 18.7	18.2	70.9 70.2	70.6	5.2 5.1	5.2		4.5 4.8	4.7		6.9 6.1	6.5	
					Bottom	5.5	25.7 25.7	25.7	8.0 8.0	8.0	20.9 20.7	20.8	70.2 70.9	70.6	5.1 5.2	5.1		8.6 8.5	8.6		6.7 7.5	7.1	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)3 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	09:29	6.6	Surface	1.0	26.3 26.3	26.3	8.1 8.0	8.1	11.2 11.2	11.2	74.5 72.7	73.6	5.6 5.5	5.6	5.5	5.2 5.2	5.2	5.5	5.6 5.6	5.6	5.6
					Middle	3.3	25.8 25.8	25.8	8.0 8.0	8.0	17.9 17.5	17.7	70.4 72.9	71.7	5.2 5.4	5.3		5.5 5.6	5.6		5.4 5.5	5.5	
					Bottom	5.6	25.9 25.7	25.8	7.9 8.0	7.9	21.0 21.3	21.2	74.0 78.3	76.2	5.3 5.7	5.5		5.7 5.9	5.8		5.1 6.4	5.8	
26-May-14	Sunny	Moderate	12:11	6.3	Surface	1.0	27.4 27.1	27.3	8.0 7.9	8.0	9.1 9.4	9.2	73.6 70.9	72.3	5.5 5.4	5.4	5.4	4.6 4.6	4.6	5.0	3.5 3.6	3.6	4.3
					Middle	3.2	26.6 26.7	26.6	8.0 7.9	7.9	14.4 14.0	14.2	71.3 70.5	70.9	5.3 5.2	5.3		4.7 4.7	4.7		4.4 4.7	4.6	
					Bottom	5.3	26.8 26.1	26.5	7.9 7.9	7.9	14.5 14.6	14.5	72.2 73.5	72.9	5.3 5.3	5.3		5.6 5.8	5.7		4.6 4.5	4.6	
28-May-14	Sunny	Moderate	12:50	7.2	Surface	1.0	26.8 27.1	27.0	8.1 8.1	8.1	19.6 17.1	18.3	79.3 76.4	77.9	5.7 5.5	5.6	5.5	2.7 2.7	2.7	2.9	3.0 3.4	3.2	3.9
					Middle	3.6	26.5 26.5	26.5	8.1 8.1	8.1	20.6 20.5	20.6	75.7 74.4	75.1	5.4 5.3	5.4		3.0 3.0	3.0		4.0 4.9	4.5	
					Bottom	6.2	26.4 26.6	26.5	8.1 8.1	8.1	21.8 21.5	21.6	75.1 72.9	74.0	5.4 5.2	5.3		3.1 3.0	3.1		4.2 3.7	4.0	
30-May-14	Sunny	Moderate	13:36	6.2	Surface	1.0	27.8 27.9	27.9	8.1 8.1	8.1	14.5 14.7	14.6	86.1 85.9	86.0	6.2 6.2	6.2	6.1	1.8 1.9	1.9	1.9	3.2 2.5	2.9	2.7
					Middle	3.1	27.1 27.1	27.1	8.1 8.1	8.1	17.3 17.3	17.3	82.8 81.0	81.9	6.0 5.9	5.9		1.9 1.9	1.9		2.3 2.3	2.3	
					Bottom	5.2	26.9 27.1	27.0	8.1 8.1	8.1	19.3 19.0	19.1	82.1 84.8	83.5	5.9 6.1	6.0		1.9 1.9	1.9		3.0 2.8	2.9	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)3 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	08:20	6.6	Surface	1.0	24.0 24.0	24.0	8.2 8.2	8.2	25.2 25.4	25.3	87.7 86.1	86.9	6.4 6.3	6.3	6.3	10.4 10.3	10.4	11.1	3.9 5.3	4.6	4.7
					Middle	3.3	23.9 23.9	23.9	8.2 8.2	8.2	27.4 27.3	27.4	86.0 88.7	87.4	6.2 6.4	6.3		11.4 11.6	11.5		4.3 4.3	4.3	
					Bottom	5.6	23.9 23.9	23.9	8.1 8.2	8.2	27.6 27.6	27.6	86.4 91.3	88.9	6.2 6.6	6.4		11.7 11.2	11.5		5.0 5.6	5.3	
5-May-14	Sunny	Moderate	09:59	6.5	Surface	1.0	24.3 24.3	24.3	8.2 8.2	8.2	23.0 22.9	22.9	88.8 90.4	89.6	6.5 6.6	6.6	6.6	4.3 4.3	4.3	5.1	2.1 2.3	2.2	2.8
					Middle	3.3	24.2 24.2	24.2	8.2 8.2	8.2	25.5 27.1	26.3	88.7 91.4	90.1	6.4 6.6	6.5		5.5 5.5	5.5		3.0 3.3	3.2	
					Bottom	5.5	24.1 24.2	24.2	8.2 8.1	8.2	28.3 28.0	28.2	94.2 89.2	91.7	6.7 6.4	6.6		5.5 5.6	5.6		2.5 3.2	2.9	
7-May-14	Cloudy	Moderate	11:49	6.5	Surface	1.0	23.5 23.5	23.5	8.2 8.2	8.2	29.8 29.8	29.8	91.4 90.5	91.0	6.6 6.5	6.5	6.5	2.9 2.8	2.9	3.2	5.3 6.7	6.0	6.2
					Middle	3.3	23.6 23.6	23.6	8.2 8.2	8.2	30.0 30.1	30.0	91.6 90.3	91.0	6.5 6.4	6.5		3.3 3.1	3.2		5.7 5.7	5.7	
					Bottom	5.5	23.6 23.7	23.7	8.2 8.2	8.2	30.2 30.5	30.4	91.2 94.5	92.9	6.5 6.7	6.6		3.3 3.4	3.4		6.7 7.0	6.9	
9-May-14	Rainy	Moderate	14:23	6.6	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	28.1 28.3	28.2	87.7 85.7	86.7	6.3 6.2	6.3	6.2	4.4 4.6	4.5	6.5	5.5 5.3	5.4	5.6
					Middle	3.3	23.7 23.7	23.7	8.2 8.2	8.2	28.9 30.0	29.5	85.2 84.7	85.0	6.1 6.0	6.1		6.0 6.7	6.4		5.8 5.3	5.6	
					Bottom	5.6	23.7 23.7	23.7	8.2 8.2	8.2	30.6 30.6	30.6	85.5 84.7	85.1	6.1 6.0	6.0		8.6 8.5	8.6		5.4 6.4	5.9	
12-May-14	Sunny	Moderate	17:26	6.6	Surface	1.0	24.9 24.9	24.9	8.0 8.0	8.0	12.9 12.9	12.9	82.5 82.9	82.7	6.4 6.4	6.4	6.3	8.3 8.1	8.2	8.5	3.1 3.3	3.2	3.8
					Middle	3.3	24.0 23.9	24.0	8.0 8.0	8.0	17.7 17.8	17.7	81.1 80.1	80.6	6.2 6.1	6.1		8.5 8.6	8.6		4.0 4.3	4.2	
					Bottom	5.6	23.8 24.2	24.0	8.0 7.9	8.0	21.5 22.0	21.8	79.7 81.6	80.7	6.0 6.0	6.0		8.7 8.7	8.7		3.8 4.2	4.0	
14-May-14	Sunny	Moderate	18:55	6.6	Surface	1.0	25.7 25.7	25.7	7.9 7.9	7.9	13.0 13.1	13.0	80.2 80.4	80.3	6.1 6.1	6.1	6.1	5.8 6.0	5.9	6.4	5.3 6.0	5.7	5.6
					Middle	3.3	25.6 25.5	25.5	7.9 7.9	7.9	15.1 15.0	15.0	80.3 80.1	80.2	6.0 6.0	6.0		6.6 6.2	6.4		4.6 4.2	4.4	
					Bottom	5.6	25.5 25.5	25.5	7.9 7.9	7.9	15.5 15.4	15.4	79.9 80.2	80.1	6.0 6.0	6.0		6.8 6.7	6.8		6.6 7.0	6.8	
16-May-14	Cloudy	Moderate	08:30	6.9	Surface	1.0	25.1 25.1	25.1	8.0 8.0	8.0	20.9 21.0	21.0	79.7 78.9	79.3	5.8 5.8	5.8	5.8	17.5 17.2	17.4	18.7	7.0 6.7	6.9	7.2
					Middle	3.5	25.0 25.0	25.0	8.0 8.0	8.0	21.3 21.3	21.3	79.8 78.8	79.3	5.8 5.8	5.8		18.4 18.6	18.5		7.4 6.8	7.1	
					Bottom	5.9	25.0 25.0	25.0	8.0 8.0	8.0	21.6 21.8	21.7	79.1 80.3	79.7	5.8 5.9	5.8		20.3 20.0	20.2		7.7 7.6	7.7	
19-May-14	Cloudy	Moderate	09:59	7.0	Surface	1.0	25.8 25.9	25.8	8.0 8.0	8.0	16.2 16.1	16.2	78.3 86.1	82.2	5.8 6.3	6.0	6.0	4.2 4.2	4.2	4.4	10.5 10.4	10.5	10.8
					Middle	3.5	25.7 25.7	25.7	8.0 8.0	8.0	18.2 18.5	18.4	76.9 81.5	79.2	5.7 6.0	5.9		4.2 4.4	4.3		10.3 10.6	10.5	
					Bottom	6.0	25.7 25.7	25.7	8.0 8.0	8.0	18.5 18.5	18.5	80.0 76.8	78.4	5.9 5.7	5.8		4.6 4.6	4.6		11.2 11.3	11.3	
21-May-14	Cloudy	Moderate	12:07	6.5	Surface	1.0	26.3 26.2	26.2	8.0 8.0	8.0	11.6 13.8	12.7	75.3 74.3	74.8	5.7 5.6	5.6	5.6	3.9 3.7	3.8	5.2	5.1 4.4	4.8	4.9
					Middle	3.3	26.1 26.0	26.1	8.0 8.0	8.0	14.5 15.1	14.8	75.5 73.8	74.7	5.6 5.5	5.6		4.4 4.9	4.7		4.8 4.5	4.7	
					Bottom	5.5	25.7 25.7	25.7	7.9 8.0	8.0	21.7 20.9	21.3	73.7 77.9	75.8	5.3 5.7	5.5		7.0 6.9	7.0		4.7 5.7	5.2	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)3 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	14:12	6.4	Surface	1.0	26.4 26.3	26.4	8.0 8.0	8.0	11.2 11.2	11.2	76.4 72.8	74.6	5.8 5.5	5.7	5.5	6.5 6.7	6.6	8.1	3.7 3.4	3.6	4.2
					Middle	3.2	26.1 26.1	26.1	8.0 8.0	8.0	17.1 16.9	17.0	72.0 70.4	71.2	5.3 5.2	5.2		8.6 8.9	8.8		5.3 3.8	4.6	
					Bottom	5.4	25.9 25.8	25.8	7.9 7.9	7.9	21.8 21.3	21.5	74.3 71.0	72.7	5.3 5.1	5.2		8.7 8.8	8.8		4.0 4.9	4.5	
26-May-14	Sunny	Moderate	17:29	6.4	Surface	1.0	27.8 27.9	27.8	7.9 7.9	7.9	9.0 8.8	8.9	76.1 78.1	77.1	5.7 5.8	5.8	5.6	6.9 6.8	6.9	6.9	5.6 5.4	5.5	5.8
					Middle	3.2	27.2 27.5	27.3	7.9 7.9	7.9	9.3 9.5	9.4	70.9 71.6	71.3	5.3 5.4	5.4		6.8 6.8	6.8		6.3 5.7	6.0	
					Bottom	5.4	26.5 26.2	26.4	7.8 7.8	7.8	17.4 18.5	18.0	72.0 72.4	72.2	5.2 5.3	5.3		6.9 6.8	6.9		6.0 5.8	5.9	
28-May-14	Sunny	Moderate	18:45	7.1	Surface	1.0	27.9 27.9	27.9	8.1 8.1	8.1	11.2 11.0	11.1	88.6 89.4	89.0	6.5 6.6	6.6	6.4	4.5 4.5	4.5	4.7	4.8 5.6	5.2	5.4
					Middle	3.6	27.2 27.6	27.4	8.0 8.1	8.1	12.7 12.4	12.5	86.0 82.5	84.3	6.2 6.1	6.1		4.8 4.5	4.7		5.5 5.7	5.6	
					Bottom	6.1	26.9 27.2	27.0	8.0 8.0	8.0	17.7 17.6	17.6	81.0 83.8	82.4	5.9 6.2	6.0		4.7 5.0	4.9		5.8 5.2	5.5	
30-May-14	Sunny	Moderate	07:29	6.5	Surface	1.0	27.2 27.3	27.3	8.2 8.2	8.2	17.6 16.9	17.3	81.1 83.5	82.3	5.8 6.0	5.9	5.8	5.6 5.5	5.6	5.8	2.3 3.7	3.0	2.9
					Middle	3.3	26.8 26.9	26.9	8.1 8.1	8.1	20.3 20.0	20.2	79.2 78.6	78.9	5.7 5.6	5.6		5.7 5.7	5.7		3.5 2.9	3.2	
					Bottom	5.5	26.7 26.7	26.7	8.1 8.1	8.1	22.2 21.8	22.0	82.6 78.7	80.7	5.8 5.6	5.7		5.9 6.1	6.0		2.8 2.4	2.6	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS4 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	14:12	16.3	Surface	1.0	24.4 24.4	24.4	8.2 8.2	8.2	26.8 26.8	26.8	92.6 92.7	92.7	6.6 6.7	6.6	6.6	7.3 7.2	7.3	7.9	4.0 3.9	4.0	4.5
					Middle	8.2	23.9 23.9	23.9	8.3 8.3	8.3	29.6 29.7	29.6	92.1 92.3	92.2	6.6 6.6	6.6		7.7 7.8	7.8		4.6 4.3	4.5	
					Bottom	15.3	23.9 24.1	24.0	8.3 8.2	8.2	29.8 29.7	29.8	91.3 91.1	91.2	6.5 6.5	6.5		8.6 8.4	8.5		5.2 4.7	5.0	
5-May-14	Sunny	Moderate	16:13	16.4	Surface	1.0	24.3 24.4	24.4	8.3 8.3	8.3	25.5 25.3	25.4	91.6 91.8	91.7	6.6 6.6	6.6	6.6	2.7 2.6	2.7	3.3	3.5 4.1	3.8	4.4
					Middle	8.2	24.2 24.2	24.2	8.3 8.3	8.3	28.8 28.8	28.8	91.0 90.9	91.0	6.5 6.5	6.5		3.6 3.5	3.6		5.2 5.4	5.3	
					Bottom	15.4	24.2 24.2	24.2	8.3 8.3	8.3	28.8 28.8	28.8	91.2 91.2	91.2	6.5 6.5	6.5		3.7 3.7	3.7		4.0 3.9	4.0	
7-May-14	Cloudy	Moderate	17:57	16.1	Surface	1.0	23.6 23.6	23.6	8.3 8.3	8.3	28.3 28.2	28.2	89.2 89.0	89.1	6.4 6.4	6.4	6.4	3.0 2.8	2.9	4.5	5.4 5.3	5.4	5.9
					Middle	8.1	23.7 23.7	23.7	8.2 8.2	8.2	30.5 30.5	30.5	88.5 88.4	88.5	6.3 6.3	6.3		5.5 5.1	5.3		6.0 5.7	5.9	
					Bottom	15.1	23.7 23.6	23.7	8.2 8.2	8.2	31.0 30.9	30.9	89.7 90.1	89.9	6.4 6.4	6.4		5.5 5.3	5.4		6.6 6.1	6.4	
9-May-14	Rainy	Moderate	10:36	16.3	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	27.5 27.4	27.4	87.8 88.4	88.1	6.4 6.4	6.4	6.3	6.5 6.2	6.4	9.0	3.4 5.0	4.2	5.6
					Middle	8.2	23.7 23.7	23.7	8.2 8.2	8.2	30.5 30.5	30.5	86.0 86.1	86.1	6.1 6.1	6.1		8.9 8.6	8.8		6.4 6.2	6.3	
					Bottom	15.3	23.7 23.7	23.7	8.2 8.2	8.2	30.5 30.5	30.5	86.2 86.3	86.3	6.1 6.1	6.1		11.8 12.0	11.9		6.5 6.2	6.4	
12-May-14	Sunny	Moderate	12:32	16.1	Surface	1.0	24.2 24.3	24.3	8.0 8.0	8.0	13.1 12.9	13.0	82.5 82.9	82.7	6.4 6.4	6.4	6.4	4.5 4.3	4.4	5.8	4.5 5.1	4.8	5.4
					Middle	8.1	23.9 23.9	23.9	8.0 8.0	8.0	16.8 16.5	16.7	82.0 81.7	81.9	6.3 6.3	6.3		6.3 6.4	6.4		6.2 6.4	6.3	
					Bottom	15.1	23.9 23.9	23.9	7.9 7.9	7.9	20.5 21.6	21.1	81.6 82.0	81.8	6.1 6.1	6.1		6.3 6.7	6.5		5.0 4.9	5.0	
14-May-14	Sunny	Moderate	13:26	16.2	Surface	1.0	25.3 25.2	25.3	8.0 8.1	8.1	17.2 17.2	17.2	85.3 84.5	84.9	6.4 6.3	6.3	6.2	6.3 6.6	6.5	10.8	4.7 4.8	4.8	6.5
					Middle	8.1	24.6 24.6	24.6	8.1 8.1	8.1	22.3 22.4	22.3	82.8 83.1	83.0	6.1 6.1	6.1		12.1 12.4	12.3		5.7 5.8	5.8	
					Bottom	15.2	24.6 24.6	24.6	8.1 8.1	8.1	22.6 22.8	22.7	82.8 83.4	83.1	6.1 6.1	6.1		13.2 13.8	13.5		9.4 8.2	8.8	
16-May-14	Cloudy	Moderate	13:15	18.3	Surface	1.0	25.2 25.2	25.2	8.1 8.1	8.1	20.4 20.4	20.4	81.7 81.9	81.8	6.0 6.0	6.0	6.0	11.3 11.1	11.2	12.1	4.0 4.0	4.0	4.6
					Middle	9.2	25.2 25.2	25.2	8.1 8.1	8.1	21.1 20.7	20.9	81.8 81.6	81.7	6.0 6.0	6.0		12.0 12.2	12.1		3.7 4.6	4.2	
					Bottom	17.3	25.2 25.1	25.1	8.0 8.0	8.0	22.6 22.6	22.6	81.5 81.8	81.7	5.9 5.9	5.9		13.0 12.8	12.9		5.3 5.7	5.5	
19-May-14	Sunny	Rough	16:17	18.0	Surface	1.0	26.8 26.7	26.8	8.1 8.1	8.1	14.4 14.3	14.4	82.8 83.0	82.9	6.1 6.1	6.1	6.0	4.2 4.2	4.2	4.3	5.0 4.4	4.7	5.7
					Middle	9.0	26.2 25.6	25.9	8.1 8.1	8.1	17.1 18.1	17.6	82.5 77.2	79.9	6.0 5.7	5.8		4.2 4.3	4.3		5.7 6.1	5.9	
					Bottom	17.0	25.6 25.6	25.6	8.1 8.1	8.1	21.4 21.1	21.3	81.0 76.9	79.0	6.0 5.6	5.8		4.4 4.5	4.5		6.9 6.3	6.6	
21-May-14	Cloudy	Moderate	17:29	17.1	Surface	1.0	26.6 26.7	26.7	8.1 8.1	8.1	12.8 12.8	12.8	79.6 80.2	79.9	5.9 6.0	6.0	5.6	4.2 3.8	4.0	6.4	5.3 5.5	5.4	5.7
					Middle	8.6	25.7 25.7	25.7	8.1 8.1	8.1	20.3 21.1	20.7	70.8 70.8	70.8	5.2 5.1	5.1		8.5 9.0	8.8		5.5 5.3	5.4	
					Bottom	16.1	25.7 25.6	25.7	8.0 8.1	8.0	21.7 22.0	21.9	76.1 72.0	74.1	5.5 5.2	5.3		6.4 6.3	6.4		5.9 6.5	6.2	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS4 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	09:57	16.3	Surface	1.0	26.4 <u>26.4</u>	26.4	8.1 <u>8.0</u>	8.1	11.0 <u>11.0</u>	11.0	74.0 <u>75.5</u>	74.8	5.6 <u>5.7</u>	5.7	5.5	6.7 <u>6.7</u>	6.7	6.9	4.8 <u>4.3</u>	4.6	4.8
					Middle	8.2	25.6 <u>25.6</u>	25.6	8.0 <u>8.0</u>	8.0	20.8 <u>21.2</u>	21.0	73.4 <u>71.5</u>	72.5	5.3 <u>5.2</u>	5.2		6.9 <u>6.8</u>	6.9		5.0 <u>4.3</u>	4.7	
					Bottom	15.3	25.6 <u>25.7</u>	25.6	7.9 <u>7.9</u>	7.9	22.0 <u>21.9</u>	22.0	66.3 <u>65.5</u>	65.9	4.8 <u>4.7</u>	4.8		7.2 <u>7.2</u>	7.2		5.6 <u>4.6</u>	5.1	
26-May-14	Sunny	Moderate	12:38	16.5	Surface	1.0	27.2 <u>27.2</u>	27.2	7.9 <u>7.9</u>	7.9	9.8 <u>9.9</u>	9.8	70.2 <u>70.0</u>	70.1	5.3 <u>5.3</u>	5.3	5.2	5.0 <u>5.2</u>	5.1	6.2	4.8 <u>4.7</u>	4.8	5.0
					Middle	8.3	26.7 <u>26.7</u>	26.7	7.9 <u>7.9</u>	7.9	14.3 <u>14.2</u>	14.2	67.9 <u>67.8</u>	67.9	5.0 <u>5.0</u>	5.0		5.4 <u>5.2</u>	5.3		4.9 <u>4.7</u>	4.8	
					Bottom	15.5	26.4 <u>26.0</u>	26.2	7.8 <u>7.8</u>	7.8	19.9 <u>20.1</u>	20.0	68.6 <u>69.0</u>	68.8	4.9 <u>5.0</u>	5.0		7.9 <u>8.3</u>	8.1		5.2 <u>5.8</u>	5.5	
28-May-14	Sunny	Moderate	13:02	18.0	Surface	1.0	27.9 <u>27.6</u>	27.7	8.1 <u>8.1</u>	8.1	14.3 <u>14.8</u>	14.6	81.9 <u>78.6</u>	80.3	5.8 <u>5.7</u>	5.8	5.7	3.0 <u>3.1</u>	3.1	3.2	3.9 <u>2.7</u>	3.3	3.6
					Middle	9.0	26.7 <u>26.5</u>	26.6	8.1 <u>8.1</u>	8.1	20.0 <u>20.5</u>	20.2	80.1 <u>74.5</u>	77.3	5.8 <u>5.3</u>	5.5		3.1 <u>3.3</u>	3.2		3.4 <u>4.4</u>	3.9	
					Bottom	17.0	26.5 <u>27.4</u>	27.0	8.1 <u>8.1</u>	8.1	22.1 <u>21.0</u>	21.6	72.3 <u>78.5</u>	75.4	5.2 <u>5.6</u>	5.4		3.3 <u>3.3</u>	3.3		3.9 <u>3.1</u>	3.5	
30-May-14	Sunny	Moderate	13:12	16.0	Surface	1.0	27.9 <u>28.2</u>	28.1	8.2 <u>8.2</u>	8.2	14.4 <u>14.2</u>	14.3	84.2 <u>88.2</u>	86.2	6.1 <u>6.4</u>	6.2	5.9	1.7 <u>1.8</u>	1.8	2.8	3.3 <u>3.3</u>	3.3	3.0
					Middle	8.0	26.8 <u>26.9</u>	26.9	8.1 <u>8.1</u>	8.1	20.4 <u>19.1</u>	19.7	76.5 <u>76.9</u>	76.7	5.5 <u>5.5</u>	5.5		3.2 <u>3.3</u>	3.3		3.8 <u>2.6</u>	3.2	
					Bottom	15.0	26.4 <u>26.4</u>	26.4	8.0 <u>8.0</u>	8.0	23.8 <u>23.5</u>	23.6	80.1 <u>78.2</u>	79.2	5.6 <u>5.5</u>	5.6		3.3 <u>3.4</u>	3.4		2.6 <u>2.3</u>	2.5	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS4 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	08:48	17.0	Surface	1.0	24.0 24.0	24.0	8.2 8.2	8.2	25.4 25.3	25.4	85.3 85.2	85.3	6.2 6.2	6.2	6.2	10.7 10.7	10.7	10.7	3.8 4.6	4.2	4.3
					Middle	8.5	23.9 23.9	23.9	8.2 8.2	8.2	27.5 27.6	27.6	84.8 84.8	84.8	6.1 6.1	6.1		10.6 10.5	10.6		3.8 4.3	4.1	
					Bottom	16.0	23.9 23.9	23.9	8.1 8.2	8.2	27.5 27.6	27.6	84.8 85.0	84.9	6.1 6.1	6.1		10.7 10.7	10.7		4.8 4.2	4.5	
5-May-14	Sunny	Moderate	10:26	17.4	Surface	1.0	24.3 24.4	24.3	8.2 8.2	8.2	22.7 22.2	22.5	87.6 87.6	87.6	6.4 6.5	6.4	6.3	5.5 5.7	5.6	6.2	2.5 2.4	2.5	2.5
					Middle	8.7	24.1 24.1	24.1	8.2 8.2	8.2	28.6 28.6	28.6	86.8 87.0	86.9	6.2 6.2	6.2		6.3 6.6	6.5		2.5 2.6	2.6	
					Bottom	16.4	24.1 24.2	24.1	8.1 8.1	8.1	28.8 28.5	28.7	87.6 87.3	87.5	6.3 6.2	6.2		6.7 6.5	6.6		2.7 2.1	2.4	
7-May-14	Cloudy	Moderate	12:16	16.9	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	29.7 29.8	29.8	88.6 88.4	88.5	6.3 6.3	6.3	6.3	4.2 4.2	4.2	5.1	5.2 6.0	5.6	5.7
					Middle	8.5	23.7 23.7	23.7	8.2 8.2	8.2	30.6 30.6	30.6	88.3 87.9	88.1	6.3 6.2	6.3		5.5 5.5	5.5		5.2 5.7	5.5	
					Bottom	15.9	23.7 23.7	23.7	8.2 8.2	8.2	30.8 30.8	30.8	88.7 89.9	89.3	6.3 6.4	6.3		5.7 5.4	5.6		6.6 5.6	6.1	
9-May-14	Rainy	Moderate	14:03	16.1	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	28.1 28.3	28.2	88.0 87.1	87.6	6.4 6.3	6.3	6.2	3.4 3.5	3.5	8.2	2.8 3.4	3.1	3.7
					Middle	8.1	23.7 23.7	23.7	8.2 8.2	8.2	30.6 30.6	30.6	84.6 84.6	84.6	6.0 6.0	6.0		9.9 9.8	9.9		3.4 3.4	3.4	
					Bottom	15.1	23.7 23.7	23.7	8.2 8.2	8.2	30.6 30.6	30.6	84.9 84.9	84.9	6.0 6.0	6.0		11.6 11.0	11.3		4.5 4.7	4.6	
12-May-14	Sunny	Moderate	16:58	16.7	Surface	1.0	24.5 24.6	24.6	8.0 8.0	8.0	14.4 13.9	14.2	81.6 82.1	81.9	6.3 6.3	6.3	6.2	6.5 6.7	6.6	7.6	3.5 3.4	3.5	3.5
					Middle	8.4	23.8 23.8	23.8	8.0 7.9	8.0	22.1 21.8	22.0	80.2 80.1	80.2	6.0 6.0	6.0		7.6 7.6	7.6		3.5 3.6	3.6	
					Bottom	15.7	23.8 23.8	23.8	7.9 7.9	7.9	22.9 22.7	22.8	80.6 81.0	80.8	6.0 6.0	6.0		8.3 8.6	8.5		3.9 3.1	3.5	
14-May-14	Sunny	Moderate	18:36	16.0	Surface	1.0	25.7 25.7	25.7	7.9 7.9	7.9	12.8 13.1	13.0	80.2 80.5	80.4	6.1 6.1	6.1	6.1	6.0 6.1	6.1	7.0	4.9 5.6	5.3	6.4
					Middle	8.0	25.5 25.2	25.4	7.9 8.0	8.0	15.4 15.6	15.5	80.5 81.1	80.8	6.0 6.1	6.0		7.0 7.3	7.2		6.8 7.2	7.0	
					Bottom	15.0	25.5 24.8	25.1	7.9 8.0	8.0	22.5 22.1	22.3	80.5 80.0	80.3	6.0 5.9	5.9		7.4 8.0	7.7		6.7 7.2	7.0	
16-May-14	Cloudy	Moderate	08:46	18.4	Surface	1.0	25.1 25.2	25.1	8.1 8.1	8.1	21.0 20.0	20.5	78.5 78.8	78.7	5.8 5.8	5.8	5.8	16.5 16.8	16.7	17.1	6.3 5.7	6.0	6.0
					Middle	9.2	25.0 25.0	25.0	8.1 8.1	8.1	21.4 21.4	21.4	78.2 78.2	78.2	5.7 5.7	5.7		17.0 16.9	17.0		5.0 5.8	5.4	
					Bottom	17.4	25.0 25.0	25.0	8.1 8.1	8.1	21.7 21.9	21.8	78.2 78.2	78.2	5.7 5.7	5.7		17.7 17.4	17.6		6.6 6.7	6.7	
19-May-14	Cloudy	Moderate	10:08	18.1	Surface	1.0	26.0 25.9	26.0	8.0 8.0	8.0	16.2 16.2	16.2	77.1 76.1	76.6	5.7 5.6	5.7	5.6	4.0 4.0	4.0	4.2	8.9 8.8	8.9	9.3
					Middle	9.1	25.8 25.6	25.7	8.0 8.0	8.0	17.4 18.6	18.0	75.6 74.3	75.0	5.6 5.5	5.5		4.1 4.2	4.2		9.6 9.0	9.3	
					Bottom	17.1	25.8 25.6	25.7	8.0 8.0	8.0	18.4 18.6	18.5	75.3 74.2	74.8	5.6 5.5	5.5		4.5 4.4	4.5		9.0 10.5	9.8	
21-May-14	Cloudy	Moderate	12:29	16.8	Surface	1.0	26.2 26.1	26.1	8.0 8.1	8.1	14.0 14.1	14.0	71.3 71.9	71.6	5.3 5.4	5.4	5.3	4.0 4.4	4.2	9.3	4.7 5.0	4.9	5.0
					Middle	8.4	25.5 25.5	25.5	8.1 8.1	8.1	22.3 22.7	22.5	71.0 71.5	71.3	5.1 5.2	5.1		11.1 11.6	11.4		3.6 4.1	3.9	
					Bottom	15.8	25.3 25.4	25.3	8.1 8.0	8.1	24.6 24.6	24.6	70.6 70.5	70.6	5.1 5.0	5.0		12.5 12.0	12.3		5.8 6.4	6.1	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS4 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	13:42	15.9	Surface	1.0	26.2 26.3	26.3	8.1 8.1	8.1	11.7 11.4	11.5	71.2 71.5	71.4	5.4 5.4	5.4	5.2	7.4 7.1	7.3	7.6	3.5 3.5	3.5	3.7
					Middle	8.0	25.7 25.6	25.7	8.0 8.0	8.0	20.2 21.8	21.0	68.7 71.5	70.1	5.0 5.1	5.0		7.5 7.4	7.5		2.6 3.6	3.1	
					Bottom	14.9	25.3 25.6	25.4	7.9 7.9	7.9	25.2 24.6	24.9	69.8 68.5	69.2	5.0 5.0	5.0		7.9 8.1	8.0		4.7 4.5	4.6	
26-May-14	Sunny	Moderate	17:01	17.3	Surface	1.0	27.9 27.8	27.9	7.9 7.9	7.9	8.8 8.9	8.9	78.2 78.4	78.3	5.8 5.9	5.9	5.6	7.8 7.9	7.9	8.2	6.5 6.7	6.6	6.9
					Middle	8.7	26.9 27.2	27.1	7.9 7.9	7.9	12.2 10.9	11.5	70.4 71.5	71.0	5.2 5.4	5.3		8.2 8.6	8.4		7.2 6.7	7.0	
					Bottom	16.3	25.8 25.9	25.9	7.8 7.8	7.8	21.6 23.3	22.5	73.2 77.5	75.4	5.3 5.5	5.4		8.3 8.5	8.4		7.3 6.7	7.0	
28-May-14	Sunny	Moderate	18:31	18.0	Surface	1.0	27.9 28.1	28.0	8.1 8.1	8.1	10.5 9.4	9.9	87.8 91.6	89.7	6.5 6.8	6.6	6.4	4.4 4.6	4.5	4.6	3.6 3.5	3.6	4.1
					Middle	9.0	27.6 27.5	27.5	8.1 8.1	8.1	12.4 12.5	12.5	87.4 82.9	85.2	6.3 6.1	6.2		4.7 4.4	4.6		3.7 4.0	3.9	
					Bottom	17.0	27.5 27.0	27.3	8.0 8.0	8.0	17.6 17.7	17.6	85.3 82.6	84.0	6.3 6.0	6.1		4.8 4.5	4.7		4.1 5.4	4.8	
30-May-14	Sunny	Moderate	07:57	16.3	Surface	1.0	27.3 27.3	27.3	8.2 8.2	8.2	15.6 14.9	15.3	80.4 80.9	80.7	5.8 5.9	5.9	5.9	4.9 4.6	4.8	4.9	2.9 3.6	3.3	3.5
					Middle	8.2	26.8 26.7	26.7	8.1 8.1	8.1	21.0 22.2	21.6	80.4 79.1	79.8	5.9 5.6	5.8		4.7 4.7	4.7		3.4 3.9	3.7	
					Bottom	15.3	26.6 27.0	26.8	8.1 8.1	8.1	22.4 22.0	22.2	77.3 75.3	76.3	5.5 5.3	5.4		5.1 5.1	5.1		3.4 3.4	3.4	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH Value	Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average		Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
2-May-14	Sunny	Moderate	15:02	13.6	Surface	1.0	24.0 24.1	24.1	8.3 8.3	8.3	28.1 27.7	27.9	85.1 85.6	85.4	6.1 6.1	6.1	6.1	4.3 4.3	4.3	4.6	5.7 5.5	5.6	6.2
					Middle	6.8	23.9 24.0	24.0	8.3 8.3	8.3	28.4 28.2	28.3	84.6 84.6	84.6	6.1 6.1	6.1	4.4 4.5	4.5		6.8 6.9	6.9		
					Bottom	12.6	23.9 23.9	23.9	8.3 8.3	8.3	28.7 28.7	28.7	84.2 84.5	84.4	6.0 6.1	6.0	5.0 4.8	4.9	6.0	5.0 4.8		6.2 6.1	6.2
5-May-14	Sunny	Moderate	17:00	13.2	Surface	1.0	24.2 24.1	24.2	8.4 8.4	8.4	26.2 26.3	26.3	91.2 91.6	91.4	6.6 6.6	6.6	6.5	2.8 2.8	2.8	2.8	3.9 3.1	3.5	3.4
					Middle	6.6	23.9 23.9	23.9	8.4 8.4	8.4	31.4 31.3	31.4	89.4 91.5	90.5	6.3 6.5	6.4	2.7 2.7	2.7		3.4 4.0	3.7		
					Bottom	12.2	23.9 23.9	23.9	8.4 8.4	8.4	31.5 31.5	31.5	94.1 90.2	92.2	6.6 6.4	6.5	2.9 2.9	2.9	6.5	2.9 2.9		3.0 2.7	2.9
7-May-14	Cloudy	Moderate	18:28	13.2	Surface	1.0	23.5 23.4	23.5	8.4 8.4	8.4	29.9 29.9	29.9	87.5 88.5	88.0	6.3 6.3	6.3	6.2	2.5 2.4	2.5	2.7	7.1 6.9	7.0	7.7
					Middle	6.6	23.7 23.7	23.7	8.4 8.4	8.4	31.8 31.5	31.7	87.3 84.6	86.0	6.2 6.0	6.1	2.6 2.7	2.7		8.5 8.3	8.4		
					Bottom	12.2	23.7 23.7	23.7	8.4 8.4	8.4	32.3 32.4	32.4	85.7 84.1	84.9	6.1 5.9	6.0	2.8 2.7	2.8	6.0	2.8 2.7		7.6 7.5	7.6
9-May-14	Rainy	Moderate	15:07	12.4	Surface	1.0	23.5 23.5	23.5	8.4 8.4	8.4	29.8 29.8	29.8	85.6 87.5	86.6	6.1 6.3	6.2	6.2	4.4 4.3	4.4	4.5	5.1 5.4	5.3	7.0
					Middle	6.2	23.6 23.6	23.6	8.4 8.4	8.4	30.2 30.2	30.2	86.1 84.2	85.2	6.1 6.0	6.1	4.5 4.5	4.5		7.9 7.8	7.9		
					Bottom	11.4	23.6 23.6	23.6	8.4 8.4	8.4	31.3 31.0	31.2	84.8 87.5	86.2	6.0 6.2	6.1	4.5 4.5	4.5	6.1	4.5 4.5		7.6 7.9	7.8
12-May-14	Sunny	Moderate	11:14	12.2	Surface	1.0	24.0 23.9	23.9	8.2 8.2	8.2	17.9 18.0	17.9	85.7 83.5	84.6	6.5 6.4	6.4	6.2	4.9 5.0	5.0	5.0	4.9 4.1	4.5	4.4
					Middle	6.1	23.7 23.6	23.6	8.2 8.2	8.2	26.4 26.6	26.5	85.3 81.9	83.6	6.1 5.9	6.0	5.0 5.0	5.0		4.6 5.0	4.8		
					Bottom	11.2	23.6 23.7	23.6	8.2 8.2	8.2	29.5 29.5	29.5	80.9 82.5	81.7	5.9 6.0	5.9	5.0 5.0	5.0	5.9	5.0 5.0		4.0 3.7	3.9
14-May-14	Sunny	Moderate	12:33	12.2	Surface	1.0	25.0 24.8	24.9	7.7 7.7	7.7	19.5 19.7	19.6	85.0 82.6	83.8	6.3 6.1	6.2	6.2	7.3 7.5	7.4	7.6	7.5 7.0	7.3	7.7
					Middle	6.1	24.2 24.2	24.2	7.7 7.7	7.7	22.3 23.1	22.7	81.1 83.5	82.3	6.0 6.1	6.1	7.7 7.8	7.8		7.8 8.0	7.9		
					Bottom	11.2	24.0 24.2	24.1	7.7 7.7	7.7	27.2 27.3	27.3	80.8 86.7	83.8	5.8 6.2	6.0	7.6 7.4	7.5	6.0	7.6 7.4		8.5 7.4	8.0
16-May-14	Cloudy	Moderate	14:32	12.5	Surface	1.0	25.4 25.5	25.5	7.7 7.6	7.6	19.4 19.3	19.4	80.8 81.7	81.3	5.9 6.0	6.0	5.9	12.5 11.4	12.0	12.1	8.3 8.7	8.5	8.3
					Middle	6.3	25.1 25.1	25.1	7.6 7.7	7.7	21.7 21.6	21.6	79.9 79.7	79.8	5.8 5.8	5.8	12.1 12.4	12.3		7.7 7.7	7.7		
					Bottom	11.5	24.9 24.8	24.8	7.6 7.6	7.6	24.5 24.4	24.5	80.1 80.1	80.1	5.8 5.8	5.8	12.1 12.1	12.1	5.8	12.1 12.1		8.7 8.8	8.8
19-May-14	Sunny	Rough	16:23	12.6	Surface	1.0	26.5 26.5	26.5	7.6 7.5	7.5	15.9 15.8	15.8	79.5 80.8	80.2	5.8 5.9	5.9	5.8	8.4 8.2	8.3	10.4	7.7 8.1	7.9	8.3
					Middle	6.3	25.0 25.1	25.1	7.6 7.5	7.6	23.8 23.4	23.6	77.8 79.1	78.5	5.6 5.7	5.7	11.4 11.3	11.4		8.4 8.2	8.3		
					Bottom	11.6	25.0 25.0	25.0	7.5 7.6	7.5	26.9 26.9	26.9	80.3 78.0	79.2	5.7 5.5	5.6	11.6 11.6	11.6	5.6	11.6 11.6		8.1 9.4	8.8
21-May-14	Cloudy	Moderate	18:22	12.1	Surface	1.0	26.7 26.9	26.8	7.6 7.6	7.6	15.0 15.0	15.0	80.5 84.3	82.4	5.9 6.2	6.1	5.9	3.3 3.2	3.3	3.3	2.8 2.6	2.7	2.5
					Middle	6.1	25.7 25.8	25.8	7.7 7.6	7.7	19.9 19.4	19.6	76.1 77.1	76.6	5.6 5.6	5.6	3.3 3.4	3.4		2.7 2.3	2.5		
					Bottom	11.1	24.9 25.0	25.0	7.7 7.6	7.7	27.9 27.8	27.8	75.8 77.1	76.5	5.4 5.5	5.4	3.4 3.2	3.3	5.4	3.4 3.2		2.6 2.1	2.4

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH Value	Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average		Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
23-May-14	Cloudy	Moderate	08:39	13.3	Surface	1.0	26.3 26.4	26.3	7.6 7.6	7.6	12.0 12.2	12.1	80.7 80.0	80.4	6.1 6.0	6.1	5.9	3.4 3.7	3.6	3.3	3.9 3.8	3.9	4.3
					Middle	6.7	25.5 25.7	25.6	7.7 7.6	7.6	22.2 21.7	21.9	77.2 79.1	78.2	5.6 5.7	5.6		3.0 2.8	2.9		3.4 4.6	4.0	
					Bottom	12.3	25.5 25.6	25.6	7.6 7.6	7.6	23.9 25.0	24.4	81.6 78.3	80.0	5.8 5.6	5.7		3.6 3.4	3.5		5.4 4.6	5.0	
26-May-14	Sunny	Moderate	11:18	13.3	Surface	1.0	26.9 26.9	26.9	7.4 7.4	7.4	12.8 13.1	12.9	82.2 83.0	82.6	6.5 6.0	6.3	5.9	4.9 4.7	4.8	4.7	5.7 5.7	5.7	5.9
					Middle	6.7	25.7 25.6	25.7	7.5 7.5	7.5	23.9 25.0	24.5	74.0 73.8	73.9	5.5 5.4	5.4		4.5 4.5	4.5		5.9 5.9	5.9	
					Bottom	12.3	25.9 25.6	25.8	7.5 7.4	7.4	25.0 25.4	25.2	70.0 71.0	70.5	5.2 5.3	5.2		4.6 5.0	4.8		5.9 6.2	6.1	
28-May-14	Sunny	Moderate	12:21	12.4	Surface	1.0	27.8 27.4	27.6	8.1 8.1	8.1	14.3 15.2	14.8	89.8 85.2	87.5	6.5 6.2	6.4	5.8	2.7 2.6	2.7	3.3	2.4 2.9	2.7	2.6
					Middle	6.2	26.4 26.2	26.3	8.0 8.1	8.0	22.2 22.5	22.4	71.6 74.5	73.1	5.1 5.2	5.1		3.8 3.6	3.7		2.7 2.2	2.5	
					Bottom	11.4	25.7 25.6	25.7	8.0 7.9	8.0	28.7 28.3	28.5	70.8 73.0	71.9	5.0 5.1	5.1		3.7 3.5	3.6		2.7 2.3	2.5	
30-May-14	Sunny	Moderate	13:40	12.4	Surface	1.0	27.7 27.7	27.7	8.3 8.3	8.3	17.2 17.2	17.2	82.9 85.1	84.0	5.9 6.1	6.0	5.7	3.1 2.9	3.0	3.2	5.6 5.2	5.4	5.6
					Middle	6.2	25.9 26.1	26.0	8.2 8.2	8.2	26.3 26.1	26.2	76.2 77.5	76.9	5.3 5.4	5.3		3.1 3.3	3.2		5.6 5.8	5.7	
					Bottom	11.4	25.8 25.8	25.8	8.2 8.2	8.2	29.1 29.0	29.0	72.4 71.9	72.2	5.1 5.0	5.1		3.5 3.3	3.4		5.0 6.1	5.6	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH Value	Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)										
						Value	Average		Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*							
2-May-14	Sunny	Moderate	07:21	13.6	Surface	1.0	23.9	23.9	8.4	8.4	26.5	26.4	87.4	87.3	6.3	6.3	6.3	3.0	3.0	3.2	2.4	2.8	3.1					
					Middle	6.8	23.9	23.9	8.4	8.4	26.8	26.7	86.8	86.9	6.3	6.3			2.9		3.0			3.6	3.5			
5-May-14	Sunny	Moderate	08:55	13.5	Surface	1.0	24.0	24.0	8.5	8.5	25.9	25.9	92.1	91.7	6.7	6.7	6.6	2.4	2.5	2.1	4.7	5.5	6.0					
					Middle	6.8	23.9	23.9	8.5	8.5	30.4	30.5	91.6	90.2	6.5	6.4			1.9		1.9			6.3	6.2			
7-May-14	Cloudy	Moderate	10:52	13.4	Surface	1.0	23.7	23.7	8.4	8.4	30.0	30.0	87.1	87.5	6.2	6.2	6.2	2.7	2.7	2.8	3.8	4.2	4.6					
					Middle	6.7	23.7	23.7	8.4	8.5	31.3	31.3	86.9	87.2	6.2	6.2			2.8		2.8			5.4	5.1			
9-May-14	Rainy	Moderate	09:23	12.2	Surface	1.0	23.5	23.5	8.4	8.4	30.7	30.7	84.2	84.7	6.0	6.0	6.0	4.7	4.6	5.3	5.8	5.8	6.1					
					Middle	6.1	23.6	23.6	8.4	8.4	31.5	31.5	84.9	84.1	6.0	6.0			5.2		5.2			5.6	6.2			
12-May-14	Sunny	Moderate	17:43	12.3	Surface	1.0	24.3	24.4	8.2	8.2	18.5	18.3	85.5	84.3	6.4	6.4	6.1	5.5	5.5	5.7	5.7	6.5	7.1					
					Middle	6.2	23.6	23.6	8.2	8.2	27.8	28.2	82.2	79.0	5.9	5.7			5.7		5.7			7.6	7.4			
14-May-14	Sunny	Moderate	19:50	12.9	Surface	1.0	25.4	25.3	7.7	7.7	18.6	18.8	86.7	85.8	6.4	6.3	6.2	6.0	6.1	6.3	5.7	5.9	6.4					
					Middle	6.5	24.7	24.7	7.7	7.7	23.4	23.5	82.9	82.9	6.0	6.0			6.2		6.2			6.4	6.7			
16-May-14	Cloudy	Moderate	06:41	12.8	Surface	1.0	24.9	24.9	7.7	7.7	23.1	22.2	82.1	81.8	6.0	6.0	5.9	9.2	9.4	10.1	5.8	5.2	5.9					
					Middle	6.4	24.3	24.3	7.8	7.7	27.8	27.8	80.1	81.0	5.7	5.8			10.2		10.2			6.2	6.4			
19-May-14	Cloudy	Moderate	09:02	12.5	Surface	1.0	25.9	26.0	7.6	7.6	14.7	14.6	78.2	77.7	5.9	5.8	5.9	3.9	3.9	4.8	4.8	5.2	7.3					
					Middle	6.3	25.3	25.3	7.7	7.7	23.9	23.7	79.6	82.1	5.7	5.9			5.2		5.2			7.8	7.9			
21-May-14	Cloudy	Moderate	10:56	12.7	Surface	1.0	26.0	26.0	7.6	7.7	14.7	14.7	77.7	77.3	5.8	5.8	5.7	3.5	3.5	3.6	3.4	3.4	4.6					
					Middle	6.4	25.3	25.4	7.7	7.7	22.2	22.0	76.9	75.9	5.4	5.5			3.6		3.7			4.5	5.2			

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS(Mf)5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH Value	Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average		Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
23-May-14	Cloudy	Moderate	14:29	13.5	Surface	1.0	26.3 26.3	26.3	7.6 7.6	7.6	13.6 13.7	13.6	80.9 79.1	80.0	6.1 5.9	6.0	5.7	3.6 3.6	3.6	4.4	3.7 3.6	3.7	3.7
					Middle	6.8	25.6 25.5	25.5	7.7 7.7	7.7	23.6 23.8	23.7	73.0 74.1	73.6	5.2 5.3	5.3		4.3 4.6	4.5		3.3 4.0	3.7	
					Bottom	12.5	25.4 25.7	25.5	7.6 7.6	7.6	24.5 24.5	24.5	74.1 78.4	76.3	5.3 5.6	5.4	4.7 5.3	5.0	3.9 3.6	3.8			
26-May-14	Sunny	Moderate	18:34	13.5	Surface	1.0	28.1 28.0	28.1	7.6 7.7	7.6	12.5 12.6	12.6	89.7 89.4	89.6	6.5 6.5	6.5	6.0	3.6 3.5	3.6	4.7	3.5 4.2	3.9	3.8
					Middle	6.8	25.7 25.7	25.7	7.6 7.5	7.5	24.3 24.9	24.6	77.2 75.0	76.1	5.5 5.4	5.4		4.4 4.9	4.7		3.6 3.6	3.6	
					Bottom	12.5	25.6 25.7	25.6	7.5 7.5	7.5	25.6 25.5	25.5	73.8 68.2	71.0	5.2 4.9	5.0	5.7 5.6	5.7	3.9 4.0	4.0			
28-May-14	Sunny	Moderate	20:02	12.8	Surface	1.0	27.7 27.8	27.8	8.4 8.4	8.4	16.5 16.0	16.2	97.1 98.4	97.8	7.0 7.1	7.0	6.2	2.6 2.5	2.6	2.9	2.8 2.4	2.6	3.6
					Middle	6.4	26.7 26.3	26.5	8.3 8.2	8.2	22.3 22.9	22.6	77.3 75.6	76.5	5.5 5.3	5.4		2.9 2.9	2.9		3.7 4.8	3.7	
					Bottom	11.8	26.1 26.1	26.1	8.2 8.2	8.2	24.4 24.2	24.3	77.3 70.7	74.0	5.5 5.0	5.2	3.1 3.1	3.1	4.8 4.1	4.5			
30-May-14	Sunny	Moderate	06:21	13.4	Surface	1.0	27.3 27.3	27.3	8.3 8.3	8.3	18.2 18.3	18.2	85.3 82.2	83.8	6.1 5.9	6.0	5.6	2.2 2.2	2.2	2.4	2.8 2.8	2.8	3.5
					Middle	6.7	25.7 25.6	25.6	8.3 8.3	8.3	27.8 28.2	28.0	74.8 73.6	74.2	5.2 5.1	5.1		2.3 2.4	2.4		4.4 4.1	4.3	
					Bottom	12.4	25.5 25.5	25.5	8.2 8.2	8.2	29.8 30.0	29.9	70.2 70.8	70.5	4.9 4.9	4.9	2.6 2.5	2.6	3.4 3.4	3.4			

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	15:51	10.3	Surface	1.0	24.2 24.1	24.2	8.2 8.2	8.2	28.0 28.1	28.0	88.2 88.7	88.5	6.3 6.4	6.3	6.3	2.1 2.1	2.1	2.2	2.5 3.6	3.1	3.0
					Middle	5.2	23.9 23.8	23.9	8.2 8.2	8.2	28.5 29.0	28.7	87.5 89.0	88.3	6.3 6.4	6.3		2.1 2.2	2.2		2.6 2.6	2.6	
					Bottom	9.3	23.8 23.7	23.7	8.2 8.2	8.2	30.0 30.8	30.4	87.6 90.1	88.9	6.2 6.4	6.3		2.2 2.1	2.2		3.7 2.8	3.3	
5-May-14	Sunny	Moderate	17:51	10.1	Surface	1.0	24.1 24.1	24.1	8.2 8.2	8.2	26.2 26.2	26.2	93.7 92.9	93.3	6.8 6.7	6.8	6.8	1.7 1.7	1.7	1.7	3.8 3.6	3.7	3.4
					Middle	5.1	24.1 24.1	24.1	8.2 8.2	8.2	27.2 27.5	27.4	93.3 92.4	92.9	6.7 6.6	6.7		1.7 1.6	1.7		2.3 3.0	2.7	
					Bottom	9.1	24.1 24.0	24.1	8.2 8.2	8.2	29.4 29.1	29.3	92.9 93.6	93.3	6.6 6.7	6.6		1.7 1.7	1.7		4.3 3.2	3.8	
7-May-14	Cloudy	Moderate	19:42	9.7	Surface	1.0	23.5 23.5	23.5	8.2 8.2	8.2	30.7 30.7	30.7	87.6 88.1	87.9	6.2 6.3	6.3	6.3	1.8 1.8	1.8	1.9	3.9 5.0	4.5	4.4
					Middle	4.9	23.5 23.6	23.6	8.2 8.2	8.2	31.1 31.0	31.0	87.4 85.8	86.6	6.2 6.1	6.2		1.9 1.9	1.9		4.0 4.0	4.0	
					Bottom	8.7	23.6 23.6	23.6	8.2 8.2	8.2	32.0 32.1	32.1	87.2 86.5	86.9	6.2 6.1	6.1		1.9 1.9	1.9		5.4 4.2	4.8	
9-May-14	Rainy	Moderate	08:50	9.5	Surface	1.0	23.5 23.5	23.5	8.2 8.2	8.2	32.1 32.1	32.1	84.0 83.6	83.8	5.9 5.9	5.9	5.9	1.2 1.3	1.3	1.7	5.3 5.7	5.5	6.8
					Middle	4.8	23.5 23.5	23.5	8.2 8.2	8.2	32.5 32.4	32.4	82.6 83.0	82.8	5.8 5.9	5.8		1.6 1.6	1.6		5.6 5.3	5.5	
					Bottom	8.5	23.5 23.5	23.5	8.2 8.2	8.2	32.5 32.5	32.5	83.2 82.7	83.0	5.9 5.8	5.9		2.1 2.0	2.1		9.8 8.9	9.4	
12-May-14	Sunny	Moderate	10:42	10.2	Surface	1.0	23.9 23.9	23.9	8.1 8.1	8.1	17.5 17.5	17.5	84.4 85.0	84.7	6.5 6.5	6.5	6.4	2.8 3.0	2.9	3.0	4.8 4.6	4.7	4.4
					Middle	5.1	23.7 23.7	23.7	8.1 8.1	8.1	23.2 23.0	23.1	83.5 83.8	83.7	6.2 6.2	6.2		2.8 2.7	2.8		3.3 4.0	3.7	
					Bottom	9.2	23.7 23.7	23.7	8.0 8.0	8.0	25.5 26.0	25.8	84.3 83.3	83.8	6.2 6.1	6.1		3.3 3.3	3.3		5.6 4.2	4.9	
14-May-14	Sunny	Moderate	11:47	9.6	Surface	1.0	25.0 25.0	25.0	8.0 8.0	8.0	18.1 18.1	18.1	84.9 85.2	85.1	6.3 6.4	6.3	6.2	4.2 3.9	4.1	4.1	4.5 3.1	3.8	4.4
					Middle	4.8	24.6 24.6	24.6	8.0 8.0	8.0	22.1 22.0	22.1	82.4 82.4	82.4	6.1 6.1	6.1		3.8 4.0	3.9		4.9 4.7	4.8	
					Bottom	8.6	24.3 24.3	24.3	8.0 8.0	8.0	24.9 24.8	24.9	82.3 82.3	82.3	6.0 6.0	6.0		4.2 4.2	4.2		4.5 4.7	4.6	
16-May-14	Cloudy	Moderate	14:24	10.1	Surface	1.0	25.4 25.4	25.4	8.1 8.1	8.1	16.8 16.7	16.8	80.8 80.8	80.8	6.0 6.0	6.0	6.0	16.1 16.4	16.3	16.9	3.4 3.7	3.6	4.0
					Middle	5.1	25.1 25.1	25.1	8.1 8.1	8.1	20.9 21.0	20.9	80.0 80.6	80.3	5.9 5.9	5.9		16.9 17.0	17.0		4.2 3.1	3.7	
					Bottom	9.1	25.1 25.1	25.1	8.0 8.0	8.0	21.7 21.7	21.7	80.3 80.8	80.6	5.9 5.9	5.9		17.6 17.4	17.5		4.4 5.0	4.7	
19-May-14	Sunny	Rough	17:21	10.2	Surface	1.0	26.0 26.1	26.1	8.1 8.1	8.1	15.5 14.9	15.2	78.4 82.6	80.5	5.7 6.1	5.9	5.9	2.9 3.0	3.0	3.2	4.3 3.9	4.1	4.5
					Middle	5.1	25.8 25.9	25.8	8.0 8.1	8.1	18.3 17.2	17.8	77.3 79.3	78.3	5.7 5.9	5.8		3.2 3.3	3.3		3.6 4.4	4.0	
					Bottom	9.2	25.7 26.1	25.9	8.1 8.0	8.1	19.1 18.9	19.0	78.7 77.1	77.9	5.9 5.7	5.8		3.3 3.3	3.3		5.5 5.1	5.3	
21-May-14	Cloudy	Moderate	19:12	9.9	Surface	1.0	27.0 27.1	27.1	8.1 8.1	8.1	14.0 13.9	14.0	82.6 84.0	83.3	6.1 6.2	6.1	6.0	1.9 1.9	1.9	1.9	3.4 2.8	3.1	4.1
					Middle	5.0	26.0 26.0	26.0	8.1 8.1	8.1	18.4 18.5	18.5	78.7 78.6	78.7	5.8 5.8	5.8		1.9 1.9	1.9		3.6 2.7	3.2	
					Bottom	8.9	26.0 26.0	26.0	8.0 8.1	8.1	18.7 18.9	18.8	80.0 79.8	79.9	5.8 5.8	5.8		2.0 2.0	2.0		5.4 6.6	6.0	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	08:07	10.1	Surface	1.0	26.4 26.4	26.4	8.1 8.1	8.1	11.0 11.5	11.2	80.7 80.5	80.6	6.1 6.1	6.1	5.9	1.5 1.5	1.5	1.6	4.2 4.9	4.6	4.7
					Middle	5.1	25.8 25.7	25.7	8.1 8.1	8.1	18.4 18.7	18.6	78.2 77.2	77.7	5.7 5.7	5.7		1.6 1.6	1.6		3.9 5.5	4.7	
					Bottom	9.1	25.5 25.6	25.5	8.0 8.0	8.0	24.2 23.8	24.0	77.5 79.1	78.3	5.5 5.7	5.6		1.6 1.8	1.7		5.0 4.5	4.8	
26-May-14	Sunny	Moderate	10:42	10.3	Surface	1.0	26.8 26.7	26.7	8.0 8.0	8.0	14.8 14.2	14.5	70.2 69.7	70.0	5.2 5.2	5.2	5.1	1.4 1.4	1.4	1.5	3.7 4.3	4.0	4.6
					Middle	5.2	26.3 26.3	26.3	8.0 8.0	8.0	19.7 19.9	19.8	69.2 69.2	69.2	5.0 5.1	5.0		1.5 1.4	1.5		4.1 4.7	4.4	
					Bottom	9.3	26.2 26.2	26.2	8.0 8.0	8.0	20.3 20.4	20.4	69.1 68.7	68.9	5.0 5.0	5.0		1.5 1.5	1.5		5.3 5.3	5.3	
28-May-14	Sunny	Moderate	11:56	10.1	Surface	1.0	27.6 27.9	27.7	8.1 8.1	8.1	13.1 13.2	13.1	83.6 83.4	83.5	6.0 6.1	6.0	6.0	1.4 1.4	1.4	1.4	2.0 2.3	2.2	2.5
					Middle	5.1	27.1 26.7	26.9	8.1 8.0	8.0	15.4 18.1	16.8	83.1 80.0	81.6	6.1 5.7	5.9		1.4 1.4	1.4		3.3 2.2	2.8	
					Bottom	9.1	26.4 26.4	26.4	8.0 8.0	8.0	21.3 21.3	21.3	79.9 76.4	78.2	5.8 5.5	5.7		1.4 1.5	1.5		2.6 2.1	2.4	
30-May-14	Sunny	Moderate	14:52	10.2	Surface	1.0	27.3 27.1	27.2	8.2 8.2	8.2	19.0 19.4	19.2	81.1 79.3	80.2	5.8 5.7	5.7	5.5	1.9 1.9	1.9	2.3	3.5 3.6	3.6	3.9
					Middle	5.1	26.0 26.1	26.0	8.1 8.1	8.1	25.9 26.1	26.0	72.8 76.1	74.5	5.1 5.3	5.2		2.4 2.4	2.4		4.4 3.3	3.9	
					Bottom	9.2	25.9 25.9	25.9	8.1 8.1	8.1	27.1 27.2	27.2	71.9 72.8	72.4	5.0 5.1	5.1		2.5 2.5	2.5		4.8 3.6	4.2	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	07:11	10.6	Surface	1.0	23.9 23.9	23.9	8.2 8.2	8.2	28.1 27.9	28.0	86.0 85.9	86.0	6.2 6.2	6.2	6.2	1.8 1.8	1.8	1.8	2.9 2.6	2.8	3.2
					Middle	5.3	23.8 23.8	23.8	8.2 8.2	8.2	28.6 28.9	28.7	85.8 85.7	85.8	6.2 6.1	6.1		1.8 1.7	1.8		3.3 3.7	3.5	
					Bottom	9.6	23.8 23.8	23.8	8.2 8.2	8.2	28.9 28.9	28.9	85.6 85.6	85.6	6.1 6.1	6.1		1.8 1.8	1.8		2.7 3.7	3.2	
5-May-14	Sunny	Moderate	08:49	10.8	Surface	1.0	24.1 24.1	24.1	8.2 8.2	8.2	26.3 26.6	26.5	90.1 90.0	90.1	6.5 6.5	6.5	6.4	1.7 1.7	1.7	1.8	3.1 2.9	3.0	3.1
					Middle	5.4	23.9 23.9	23.9	8.2 8.2	8.2	30.0 30.4	30.2	88.7 88.8	88.8	6.3 6.3	6.3		1.8 1.8	1.8		3.2 3.3	3.3	
					Bottom	9.8	23.9 23.9	23.9	8.2 8.2	8.2	30.4 30.3	30.4	89.4 89.2	89.3	6.3 6.3	6.3		1.8 1.9	1.9		3.7 2.5	3.1	
7-May-14	Cloudy	Moderate	10:36	10.6	Surface	1.0	23.5 23.5	23.5	8.2 8.2	8.2	30.9 30.8	30.8	87.0 87.5	87.3	6.2 6.2	6.2	6.2	1.6 1.6	1.6	1.7	4.6 4.0	4.3	4.6
					Middle	5.3	23.5 23.6	23.6	8.2 8.2	8.2	31.6 31.8	31.7	86.3 86.6	86.5	6.1 6.1	6.1		1.8 1.7	1.8		4.7 5.1	4.9	
					Bottom	9.6	23.6 23.5	23.6	8.2 8.2	8.2	31.9 31.8	31.8	86.9 87.1	87.0	6.1 6.2	6.2		1.8 1.8	1.8		4.1 5.1	4.6	
9-May-14	Rainy	Moderate	15:43	9.9	Surface	1.0	23.5 23.5	23.5	8.1 8.1	8.1	30.1 30.1	30.1	89.0 88.3	88.7	6.4 6.3	6.3	6.3	3.4 3.4	3.4	3.0	6.4 6.4	6.4	6.9
					Middle	5.0	23.5 23.5	23.5	8.1 8.1	8.1	30.4 30.5	30.5	88.7 87.0	87.9	6.3 6.2	6.3		3.0 2.8	2.9		7.5 6.9	7.2	
					Bottom	8.9	23.6 23.5	23.6	8.1 8.1	8.1	30.9 30.6	30.7	87.4 89.8	88.6	6.2 6.4	6.3		2.4 2.7	2.6		7.1 7.2	7.2	
12-May-14	Sunny	Moderate	18:42	10.1	Surface	1.0	24.5 24.6	24.5	8.0 8.0	8.0	17.8 17.7	17.7	85.1 87.3	86.2	6.4 6.6	6.5	6.4	2.9 2.8	2.9	3.1	4.3 3.9	4.1	4.2
					Middle	5.1	24.3 23.8	24.1	8.1 8.0	8.1	19.1 20.7	19.9	85.2 81.4	83.3	6.4 6.1	6.3		3.2 3.1	3.2		4.2 4.3	4.3	
					Bottom	9.1	23.6 23.8	23.7	8.0 8.0	8.0	27.8 26.7	27.3	80.9 84.3	82.6	5.9 6.1	6.0		3.2 3.2	3.2		4.7 3.5	4.1	
14-May-14	Sunny	Moderate	20:17	10.2	Surface	1.0	25.4 25.3	25.3	8.0 8.0	8.0	18.1 18.6	18.3	85.0 85.5	85.3	6.3 6.3	6.3	6.3	4.5 4.7	4.6	4.8	5.8 5.9	5.9	5.7
					Middle	5.1	24.9 24.9	24.9	8.1 8.0	8.1	20.1 20.3	20.2	83.1 85.2	84.2	6.1 6.3	6.2		5.0 5.0	5.0		5.5 6.3	5.9	
					Bottom	9.2	24.7 24.6	24.6	8.0 8.0	8.0	22.3 23.0	22.6	83.4 88.4	85.9	6.1 6.5	6.3		4.9 4.8	4.9		5.3 5.5	5.4	
16-May-14	Cloudy	Moderate	07:18	10.1	Surface	1.0	24.8 24.8	24.8	8.1 8.1	8.1	22.9 22.8	22.9	81.3 81.4	81.4	5.9 5.9	5.9	5.9	4.0 3.9	4.0	4.1	5.8 6.0	5.9	5.1
					Middle	5.1	24.7 24.7	24.7	8.1 8.1	8.1	24.6 24.5	24.5	81.2 81.0	81.1	5.9 5.9	5.9		4.0 4.1	4.1		5.0 4.8	4.9	
					Bottom	9.1	24.7 24.7	24.7	8.1 8.1	8.1	25.0 25.3	25.1	81.3 80.8	81.1	5.9 5.8	5.8		4.3 4.3	4.3		4.5 4.4	4.5	
19-May-14	Cloudy	Moderate	08:47	10.1	Surface	1.0	26.0 26.0	26.0	8.0 8.0	8.0	14.7 14.5	14.6	74.6 73.6	74.1	5.5 5.5	5.5	5.5	2.7 2.9	2.8	3.0	7.3 7.0	7.2	7.9
					Middle	5.1	25.9 25.9	25.9	8.0 8.0	8.0	16.6 16.5	16.6	74.0 73.2	73.6	5.5 5.5	5.5		3.0 3.0	3.0		7.1 6.3	6.7	
					Bottom	9.1	25.7 25.9	25.8	8.0 7.9	8.0	19.9 17.6	18.7	73.4 73.1	73.3	5.4 5.4	5.4		3.1 3.1	3.1		10.0 9.3	9.7	
21-May-14	Cloudy	Moderate	10:47	10.3	Surface	1.0	26.1 26.1	26.1	8.1 8.0	8.1	14.0 14.0	14.0	77.9 78.3	78.1	5.8 5.9	5.9	5.8	2.6 2.7	2.7	2.2	4.3 3.7	4.0	5.3
					Middle	5.2	25.6 26.0	25.8	8.1 8.1	8.1	21.4 21.8	21.6	76.0 76.9	76.5	5.5 5.7	5.6		1.9 2.2	2.1		5.3 4.5	4.9	
					Bottom	9.3	25.6 24.9	25.3	8.0 8.1	8.1	28.4 28.4	28.4	76.8 74.9	75.9	5.5 5.3	5.4		1.7 1.6	1.7		7.4 6.3	6.9	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CS6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	15:31	10.0	Surface	1.0	26.3 26.2	26.2	8.1 8.1	8.1	13.2 13.4	13.3	82.4 78.7	80.6	6.2 5.9	6.0	5.8	2.1 2.1	2.1	2.1	3.8 3.7	3.8	3.4
					Middle	5.0	25.6 25.6	25.6	8.1 8.1	8.1	19.3 20.1	19.7	74.8 74.8	74.8	5.5 5.5	5.5		2.1 2.1	2.1		2.9 3.9	3.4	
					Bottom	9.0	24.8 25.0	24.9	7.9 7.9	7.9	30.2 30.1	30.1	75.4 76.6	76.0	5.3 5.3	5.3		2.1 2.0	2.1		3.5 2.2	2.9	
26-May-14	Sunny	Moderate	18:52	10.1	Surface	1.0	27.4 27.6	27.5	8.1 8.1	8.1	14.8 14.8	14.8	77.1 82.3	79.7	5.6 6.0	5.8	5.7	2.2 2.2	2.2	2.2	3.1 3.2	3.2	3.2
					Middle	5.1	26.7 26.8	26.7	8.1 8.1	8.1	18.8 17.7	18.3	76.2 75.9	76.1	5.4 5.5	5.5		2.2 2.2	2.2		3.3 2.9	3.1	
					Bottom	9.1	25.4 26.1	25.8	8.1 8.0	8.1	26.2 26.1	26.2	67.6 71.1	69.4	4.8 5.1	5.0		2.2 2.3	2.3		3.3 3.5	3.4	
28-May-14	Sunny	Moderate	19:40	10.1	Surface	1.0	27.8 27.7	27.7	8.3 8.3	8.3	16.7 16.9	16.8	105.2 104.4	104.8	7.5 7.5	7.5	7.4	1.1 1.2	1.2	1.2	3.0 2.8	2.9	3.3
					Middle	5.1	27.2 27.6	27.4	8.2 8.2	8.2	17.5 17.3	17.4	103.5 100.3	101.9	7.3 7.2	7.3		1.1 1.2	1.2		4.1 2.7	3.4	
					Bottom	9.1	27.2 27.3	27.3	8.2 8.2	8.2	19.6 19.9	19.7	99.3 99.4	99.4	7.1 7.2	7.1		1.2 1.1	1.2		3.4 3.6	3.5	
30-May-14	Sunny	Moderate	06:15	10.1	Surface	1.0	26.8 27.1	27.0	8.1 8.1	8.1	16.8 16.6	16.7	75.4 77.0	76.2	5.5 5.6	5.5	5.4	1.3 1.3	1.3	1.4	4.3 4.3	4.3	3.8
					Middle	5.1	26.3 26.4	26.4	8.1 8.1	8.1	23.4 21.9	22.7	72.8 73.9	73.4	5.2 5.3	5.2		1.4 1.3	1.4		3.5 4.0	3.8	
					Bottom	9.1	25.9 26.3	26.1	8.0 8.0	8.0	27.9 27.7	27.8	73.4 75.0	74.2	5.1 5.2	5.1		1.4 1.3	1.4		2.6 4.1	3.4	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CSA - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH Value	Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average		Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
2-May-14	Sunny	Moderate	16:01	34.9	Surface	1.0	24.2 24.2	24.2	8.2 8.2	8.2	27.9 27.9	27.9	88.4 88.4	88.4	6.3 6.3	6.3	6.3	2.1 2.1	2.1	2.1	2.6 2.9	2.8	3.0
					Middle	17.5	23.6 23.6	23.6	8.2 8.2	8.2	31.6 31.2	31.4	86.6 87.0	86.8	6.1 6.2	6.2	2.1 2.1	2.1	2.6 3.0	2.8			
					Bottom	33.9	23.6 23.6	23.6	8.2 8.2	8.2	31.5 31.5	31.5	86.9 86.9	86.9	6.2 6.2	6.2	2.1 2.1	2.1	3.6 3.2	3.4			
5-May-14	Sunny	Moderate	18:01	34.8	Surface	1.0	24.0 24.1	24.1	8.3 8.3	8.3	26.9 26.2	26.6	90.4 91.4	90.9	6.5 6.6	6.6	6.5	1.6 1.6	1.6	1.7	3.0 2.6	2.8	3.7
					Middle	17.4	23.8 23.8	23.8	8.3 8.3	8.3	31.7 31.6	31.7	89.5 90.0	89.8	6.3 6.3	6.3	1.7 1.8	1.8	3.5 5.2	4.4			
					Bottom	33.8	23.8 23.9	23.8	8.2 8.2	8.2	32.0 31.5	31.7	90.3 91.2	90.8	6.4 6.4	6.4	1.8 1.8	1.8	3.8 4.0	3.9			
7-May-14	Cloudy	Moderate	19:52	34.1	Surface	1.0	23.4 23.5	23.5	8.3 8.3	8.3	30.5 30.5	30.5	86.0 85.3	85.7	6.1 6.1	6.1	6.0	1.8 1.7	1.8	1.8	4.3 4.3	4.3	4.4
					Middle	17.1	23.6 23.6	23.6	8.2 8.2	8.2	32.3 32.3	32.3	83.8 83.9	83.9	5.9 5.9	5.9	1.7 1.7	1.7	4.0 4.4	4.2			
					Bottom	33.1	23.6 23.6	23.6	8.2 8.2	8.2	32.4 32.5	32.5	85.6 84.5	85.1	6.0 6.0	6.0	1.8 1.8	1.8	5.0 4.6	4.8			
9-May-14	Rainy	Moderate	08:35	34.4	Surface	1.0	23.5 23.5	23.5	8.2 8.2	8.2	32.1 32.1	32.1	84.7 83.9	84.3	6.0 5.9	6.0	5.9	1.2 1.3	1.3	1.7	7.4 6.1	6.8	8.6
					Middle	17.2	23.5 23.5	23.5	8.2 8.2	8.2	32.5 32.5	32.5	83.1 82.4	82.8	5.9 5.8	5.8	1.8 1.7	1.8	8.8 8.1	8.5			
					Bottom	33.4	23.5 23.5	23.5	8.2 8.2	8.2	32.7 32.7	32.7	82.5 83.9	83.2	5.8 5.9	5.9	2.0 1.9	2.0	10.3 10.9	10.6			
12-May-14	Sunny	Moderate	10:33	34.8	Surface	1.0	23.9 23.9	23.9	8.1 8.1	8.1	16.4 17.0	16.7	85.0 84.8	84.9	6.5 6.5	6.5	6.3	3.0 2.9	3.0	2.8	4.3 3.6	4.0	4.8
					Middle	17.4	23.7 23.7	23.7	8.1 8.1	8.1	25.3 24.9	25.1	82.3 82.8	82.6	6.0 6.1	6.1	2.5 2.4	2.5	4.5 6.2	5.4			
					Bottom	33.8	23.7 23.6	23.6	8.1 8.0	8.0	26.9 28.8	27.8	82.8 83.4	83.1	6.0 6.0	6.0	3.1 2.9	3.0	4.8 5.0	4.9			
14-May-14	Sunny	Moderate	11:33	34.4	Surface	1.0	25.1 25.0	25.1	8.0 8.0	8.0	17.4 17.6	17.5	85.9 85.1	85.5	6.4 6.4	6.4	6.2	4.1 4.2	4.2	4.4	6.2 4.0	5.1	4.8
					Middle	17.2	24.3 24.3	24.3	8.0 8.0	8.0	24.1 24.2	24.2	81.6 82.2	81.9	6.0 6.0	6.0	4.5 4.8	4.7	4.8 4.0	4.4			
					Bottom	33.4	24.2 24.2	24.2	8.0 8.0	8.0	25.0 25.3	25.2	82.7 82.0	82.4	6.0 6.0	6.0	4.4 4.1	4.3	5.2 4.8	5.0			
16-May-14	Cloudy	Moderate	14:37	36.5	Surface	1.0	25.5 25.3	25.4	8.1 8.1	8.1	16.7 16.9	16.8	80.7 80.6	80.7	6.0 6.0	6.0	6.0	15.6 15.4	15.5	16.0	3.8 5.2	4.5	5.0
					Middle	18.3	25.2 25.1	25.1	8.1 8.1	8.1	19.3 21.1	20.2	80.3 80.3	80.3	5.9 5.9	5.9	15.8 16.0	15.9	5.9 4.9	5.4			
					Bottom	35.5	25.1 25.2	25.2	8.1 8.1	8.1	21.9 21.6	21.7	80.7 80.5	80.6	5.9 5.9	5.9	16.6 16.4	16.5	5.4 4.6	5.0			
19-May-14	Sunny	Rough	17:34	36.2	Surface	1.0	26.0 26.0	26.0	8.1 8.0	8.1	15.4 15.8	15.6	75.1 75.1	75.1	5.6 5.6	5.6	5.6	3.0 2.8	2.9	3.0	5.6 5.5	5.6	5.5
					Middle	18.1	25.7 25.7	25.7	8.1 8.0	8.0	18.3 18.0	18.2	75.0 75.1	75.1	5.5 5.5	5.5	3.0 3.0	3.0	5.4 5.2	5.3			
					Bottom	35.2	25.8 25.6	25.7	8.0 8.0	8.0	19.0 19.2	19.1	74.6 74.5	74.6	5.5 5.5	5.5	3.1 3.2	3.2	5.5 5.8	5.7			
21-May-14	Cloudy	Moderate	19:27	35.1	Surface	1.0	27.0 27.1	27.1	8.1 8.1	8.1	13.9 13.7	13.8	83.5 82.6	83.1	6.2 6.1	6.1	5.8	1.8 1.9	1.9	2.8	3.4 4.6	4.0	4.1
					Middle	17.6	25.5 25.6	25.5	8.1 8.1	8.1	22.0 21.9	21.9	76.0 75.5	75.8	5.5 5.5	5.5	2.4 2.7	2.6	4.7 3.7	4.2			
					Bottom	34.1	25.4 25.3	25.4	8.1 8.1	8.1	24.0 25.0	24.5	77.1 77.3	77.2	5.5 5.5	5.5	3.8 4.0	3.9	4.7 3.6	4.2			

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CSA - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH Value	Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average		Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
23-May-14	Cloudy	Moderate	07:59	34.9	Surface	1.0	26.4 26.4	26.4	8.1 8.1	8.1	11.2 11.5	11.4	81.2 81.4	81.3	6.1 6.1	6.1	5.8	2.5 2.5	2.5	2.6	5.6 6.0	5.8	5.6
					Middle	17.5	25.6 25.7	25.7	8.1 8.1	8.1	20.7 20.7	20.7	74.3 76.4	75.4	5.4 5.5	5.5		2.6 2.5	2.6		5.9 5.5	5.7	
					Bottom	33.9	25.0 25.0	25.0	8.0 8.0	8.0	28.2 28.3	28.3	76.0 74.5	75.3	5.4 5.2	5.3		2.6 2.5	2.6		4.8 5.8	5.3	
26-May-14	Sunny	Moderate	10:34	34.4	Surface	1.0	26.7 26.6	26.7	8.0 8.0	8.0	14.0 14.2	14.1	69.8 70.0	69.9	5.2 5.2	5.2	5.2	1.6 1.7	1.7	1.7	4.8 4.6	4.7	4.9
					Middle	17.2	26.2 26.3	26.2	8.0 8.0	8.0	20.0 19.7	19.9	69.3 69.5	69.4	5.0 5.2	5.1		1.6 1.6	1.6		4.5 5.0	4.8	
					Bottom	33.4	26.2 26.2	26.2	8.0 8.0	8.0	20.7 20.8	20.8	68.9 69.3	69.1	5.0 5.0	5.0		1.9 1.9	1.9		5.1 5.5	5.3	
28-May-14	Sunny	Moderate	11:42	36.0	Surface	1.0	27.9 28.0	27.9	8.1 8.1	8.1	13.1 13.3	13.2	88.2 82.6	85.4	6.4 6.0	6.2	6.1	1.5 1.4	1.5	1.6	2.9 2.5	2.7	3.0
					Middle	18.0	27.6 26.4	27.0	8.1 8.0	8.0	15.4 15.2	15.3	85.6 80.7	83.2	6.2 5.7	6.0		1.5 1.5	1.5		2.7 3.5	3.1	
					Bottom	35.0	27.4 26.1	26.8	8.0 7.8	7.9	21.1 21.6	21.4	84.0 72.4	78.2	6.1 5.2	5.6		1.6 1.7	1.7		3.5 3.1	3.3	
30-May-14	Sunny	Moderate	15:01	34.1	Surface	1.0	27.9 27.7	27.8	8.2 8.2	8.2	16.9 17.0	17.0	77.3 79.1	78.2	5.5 5.7	5.6	5.4	1.5 1.5	1.5	1.8	3.4 4.1	3.8	3.6
					Middle	17.1	26.1 26.0	26.1	8.1 8.1	8.1	25.9 26.4	26.2	75.5 71.0	73.3	5.2 5.1	5.2		1.7 1.6	1.7		3.9 3.4	3.7	
					Bottom	33.1	26.1 25.6	25.8	8.1 8.1	8.1	27.4 28.2	27.8	72.9 70.7	71.8	5.1 4.9	5.0		2.4 2.2	2.3		4.0 2.8	3.4	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CSA - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)			pH Value	Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)									
						Value	Average	Value		Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*							
2-May-14	Sunny	Moderate	07:03	34.5	Surface	1.0	23.9	23.9	8.2	8.2	27.1	27.3	86.8	86.6	6.3	6.2	6.2	1.6	1.6	1.8	2.2	2.9	3.0					
					Middle	17.3	23.8	23.8	8.2	8.2	29.0	29.1	85.9	86.2	6.2	6.2		1.9	1.9		3.2	3.3						
5-May-14	Sunny	Moderate	08:40	35.5	Surface	1.0	24.0	24.0	8.2	8.2	27.7	27.6	89.3	89.8	6.4	6.5	6.4	1.8	1.8	1.8	2.8	2.7	2.9					
					Middle	17.8	23.9	23.9	8.2	8.2	30.5	30.5	88.1	88.3	6.2	6.3		1.8	1.9		3.3	3.4						
7-May-14	Cloudy	Moderate	10:27	34.8	Surface	1.0	23.5	23.5	8.2	8.2	30.7	30.7	87.5	87.4	6.2	6.2	6.2	1.7	1.7	1.7	3.6	4.3	4.4					
					Middle	17.4	23.6	23.6	8.2	8.2	32.0	32.0	85.6	86.0	6.1	6.1		1.6	1.6		4.6	4.7						
9-May-14	Rainy	Moderate	16:00	34.7	Surface	1.0	23.5	23.5	8.2	8.2	30.2	30.2	87.8	87.8	6.3	6.3	6.2	3.3	3.4	2.4	5.4	5.6	6.4					
					Middle	17.4	23.5	23.5	8.2	8.2	31.6	31.6	84.4	84.6	6.0	6.0		2.0	1.9		5.6	6.4						
12-May-14	Sunny	Moderate	18:51	35.1	Surface	1.0	24.5	24.6	8.1	8.1	17.9	17.8	84.2	85.2	6.3	6.4	6.1	2.9	2.9	3.3	3.8	3.7	3.9					
					Middle	17.6	23.6	23.6	8.1	8.1	28.0	28.3	80.4	79.9	5.8	5.8		3.1	3.2		4.3	4.4						
14-May-14	Sunny	Moderate	20:31	35.0	Surface	1.0	25.4	25.3	8.0	8.0	18.1	18.7	84.7	84.0	6.3	6.2	6.1	4.5	4.7	5.0	3.8	3.8	4.9					
					Middle	17.5	24.7	24.7	8.1	8.1	21.3	21.3	81.7	81.6	6.0	6.0		5.2	5.3		4.4	5.3						
16-May-14	Cloudy	Moderate	07:01	36.6	Surface	1.0	25.0	25.0	8.1	8.1	21.9	21.9	82.0	81.8	6.0	6.0	6.0	3.5	3.5	4.0	6.6	6.0	5.9					
					Middle	18.3	24.7	24.8	8.1	8.1	24.4	23.7	81.3	81.8	5.9	5.9		3.9	4.0		6.0	6.2						
19-May-14	Cloudy	Moderate	08:24	36.1	Surface	1.0	25.9	25.8	8.1	8.1	15.6	16.5	77.8	76.9	5.7	5.6	5.6	2.8	2.8	2.9	5.9	5.5	6.7					
					Middle	18.1	25.6	25.6	8.1	8.1	19.1	19.1	77.6	76.6	5.7	5.6		2.9	2.9		5.6	5.7						
21-May-14	Cloudy	Moderate	10:33	35.4	Surface	1.0	26.1	26.1	8.1	8.1	14.1	14.1	78.7	78.0	5.9	5.8	5.5	2.7	2.8	2.6	4.6	4.8	5.6					
					Middle	17.7	24.8	24.8	8.1	8.1	28.9	28.8	75.1	74.6	5.3	5.2		2.3	2.3		5.3	5.9						

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at CSA - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH Value	Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average		Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
23-May-14	Cloudy	Moderate	15:42	34.9	Surface	1.0	26.1 26.2	26.2	8.2 8.2	8.2	13.3 13.3	13.3	75.3 77.5	76.4	5.7 5.8	5.7	5.5	2.1 2.2	2.2	2.2	3.5 2.7	3.1	3.0
					Middle	17.5	24.6 24.7	24.7	8.1 8.1	8.1	31.0 30.8	30.9	73.2 75.6	74.4	5.1 5.3	5.2		2.2 2.2	2.2		2.5 2.9	2.7	
					Bottom	33.9	24.6 24.7	24.7	8.0 8.0	8.0	31.2 30.9	31.1	69.4 70.6	70.0	4.8 4.9	4.9		4.9	2.2 2.2		2.2	2.7 3.9	
26-May-14	Sunny	Moderate	19:00	35.3	Surface	1.0	27.3 27.4	27.3	8.1 8.1	8.1	15.3 14.8	15.0	76.2 76.1	76.2	5.5 5.6	5.5	5.3	2.2 2.1	2.2	2.3	2.5 2.6	2.6	2.7
					Middle	17.7	25.6 25.8	25.7	8.1 8.1	8.1	25.5 25.3	25.4	69.9 70.1	70.0	5.1 5.1	5.1		2.2 2.3	2.3		2.3 2.7	2.5	
					Bottom	34.3	25.3 25.3	25.3	8.1 8.1	8.1	28.5 28.4	28.4	69.3 68.1	68.7	4.9 4.9	4.9		4.9	2.3 2.2		2.3	3.0 3.2	
28-May-14	Sunny	Moderate	19:56	36.1	Surface	1.0	27.8 27.8	27.8	8.3 8.3	8.3	16.7 16.5	16.6	106.7 110.3	108.5	7.7 7.9	7.8	7.7	1.1 1.1	1.1	1.2	3.3 2.4	2.9	3.6
					Middle	18.1	27.4 27.7	27.6	8.3 8.3	8.3	17.2 16.8	17.0	103.4 105.9	104.7	7.4 7.6	7.5		1.1 1.2	1.2		4.0 3.9	4.0	
					Bottom	35.1	27.3 27.1	27.2	8.3 8.2	8.3	19.5 19.3	19.4	104.9 101.1	103.0	7.5 7.3	7.4		7.4	1.2 1.2		1.2	3.7 4.2	
30-May-14	Sunny	Moderate	06:08	34.3	Surface	1.0	27.2 27.2	27.2	8.0 8.0	8.0	16.6 16.7	16.6	75.9 77.9	76.9	5.5 5.6	5.6	5.5	1.2 1.1	1.2	1.2	2.8 3.0	2.9	3.0
					Middle	17.2	26.5 25.8	26.2	8.1 8.1	8.1	22.5 25.5	24.0	74.7 74.6	74.7	5.2 5.3	5.3		1.2 1.2	1.2		4.1 2.5	3.3	
					Bottom	33.3	25.8 26.2	26.0	8.0 8.0	8.0	27.8 27.9	27.8	71.7 70.0	70.9	5.0 4.9	4.9		4.9	1.3 1.2		1.3	2.7 2.7	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-May-14	Sunny	Moderate	13:57	3.5	Surface	1.0	24.4 24.3	24.4	8.3 8.3	8.3	26.8 27.0	26.9	89.2 89.2	89.2	6.4 6.4	6.4	6.4	4.0 4.2	4.1	4.3	3.8 4.8	4.3	4.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.5	24.2 24.1	24.2	8.3 8.4	8.3	28.0 28.0	28.0	88.9 89.2	89.1	6.4 6.4	6.4		6.4	4.4 4.5		4.5	4.4 4.5		4.5	4.6 4.5	4.6	
5-May-14	Sunny	Moderate	15:53	3.4	Surface	1.0	24.3 24.4	24.4	8.4 8.4	8.4	26.3 26.2	26.3	97.2 95.7	96.5	7.0 6.9	6.9	6.9	3.8 3.4	3.6	3.9	4.3 4.0	4.2	4.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.4	24.3 24.3	24.3	8.4 8.4	8.4	27.5 27.7	27.6	99.2 96.4	97.8	7.1 6.9	7.0		7.0	4.2 3.9		4.1	4.2 3.9		4.1	4.9 4.4	4.7	
7-May-14	Cloudy	Moderate	17:25	3.3	Surface	1.0	23.0 23.0	23.0	8.4 8.4	8.4	27.5 27.4	27.5	100.1 97.8	99.0	7.3 7.2	7.2	7.2	2.2 2.2	2.2	2.3	5.2 6.2	5.7	5.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.3	23.0 23.0	23.0	8.4 8.4	8.4	27.6 27.5	27.5	98.7 97.0	97.9	7.2 7.1	7.2		7.2	2.4 2.2		2.3	2.4 2.2		2.3	6.0 5.9	6.0	
9-May-14	Rainy	Moderate	13:59	3.2	Surface	1.0	23.2 23.2	23.2	8.3 8.4	8.3	27.3 27.3	27.3	94.6 94.3	94.5	6.9 6.9	6.9	6.9	5.4 5.4	5.4	5.5	5.1 6.5	5.8	7.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.2	23.2 23.2	23.2	8.4 8.3	8.3	27.3 27.4	27.3	94.3 96.0	95.2	6.9 7.0	7.0		7.0	5.4 5.7		5.6	5.4 5.7		5.6	8.0 8.7	8.4	
12-May-14	Sunny	Moderate	12:22	3.2	Surface	1.0	24.2 24.5	24.4	8.2 8.2	8.2	16.1 16.8	16.5	89.8 90.1	90.0	6.9 6.8	6.8	6.8	5.0 5.1	5.1	5.2	5.3 5.0	5.2	5.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.2	24.2 23.8	24.0	8.2 8.2	8.2	21.2 21.7	21.4	89.6 89.3	89.5	6.7 6.7	6.7		6.7	5.1 5.3		5.2	5.1 5.3		5.2	5.9 5.4	5.7	
14-May-14	Sunny	Moderate	13:47	3.1	Surface	1.0	25.0 25.3	25.1	7.7 7.7	7.7	21.9 21.2	21.6	85.8 85.4	85.6	6.3 6.2	6.2	6.2	11.4 11.4	11.4	11.5	7.2 6.2	6.7	6.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.1	25.1 24.8	25.0	7.7 7.6	7.7	21.5 22.8	22.2	85.4 90.9	88.2	6.2 6.6	6.4		6.4	11.4 11.5		11.5	11.4 11.5		11.5	7.0 5.1	6.1	
16-May-14	Cloudy	Moderate	13:05	3.1	Surface	1.0	26.0 26.0	26.0	7.6 7.6	7.6	19.7 19.8	19.8	89.9 90.2	90.1	6.5 6.5	6.5	6.5	7.3 7.5	7.4	7.5	5.4 4.0	4.7	5.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.1	25.8 26.0	25.9	7.6 7.6	7.6	20.7 20.2	20.4	89.5 89.9	89.7	6.5 6.5	6.5		6.5	7.5 7.5		7.5	7.5 7.5		7.5	5.4 6.2	5.8	
19-May-14	Sunny	Rough	15:16	3.2	Surface	1.0	26.9 26.9	26.9	7.5 7.5	7.5	18.2 18.3	18.3	90.6 89.8	90.2	6.5 6.5	6.5	6.5	7.1 7.3	7.2	7.2	8.0 8.9	8.5	9.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.2	26.8 26.6	26.7	7.5 7.5	7.5	18.5 18.6	18.6	90.2 91.0	90.6	6.5 6.6	6.5		6.5	7.2 7.2		7.2	7.2 7.2		7.2	9.6 9.4	9.5	
21-May-14	Cloudy	Moderate	17:15	3.1	Surface	1.0	27.2 27.0	27.1	7.7 7.6	7.7	15.9 16.1	16.0	95.7 94.1	94.9	7.0 6.9	6.9	6.9	4.2 4.0	4.1	4.0	5.4 5.3	5.4	6.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.1	26.8 26.9	26.9	7.6 7.6	7.6	16.6 16.5	16.6	93.6 94.2	93.9	6.8 6.9	6.8		6.8	3.9 3.9		3.9	3.9 3.9		3.9	6.6 6.8	6.7	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-May-14	Cloudy	Moderate	09:49	3.2	Surface	1.0	26.2 26.3	26.2	7.6 7.6	7.6	18.7 18.2	18.5	74.9 80.9	77.9	5.5 5.9	5.7	5.7	18.0 17.8	17.9	18.5	5.9 6.6	6.3	6.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	26.2 26.0	26.1	7.4 7.6	7.5	20.7 20.5	20.6	88.2 76.1	82.2	6.4 5.5	5.9		18.9 19.2	19.1		6.6 5.4	6.0				
26-May-14	Sunny	Moderate	12:26	3.1	Surface	1.0	28.1 27.8	28.0	7.7 7.7	7.7	14.2 14.2	14.2	95.3 95.8	95.6	6.9 7.0	6.9	6.9	5.1 5.0	5.1	6.5	3.4 3.6	3.5	5.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.1	27.5 26.9	27.2	7.6 7.6	7.6	18.3 19.9	19.1	96.4 92.9	94.7	6.9 6.6	6.8		7.8 8.0	7.9		6.2 7.1	6.7				
28-May-14	Sunny	Moderate	13:40	2.9	Surface	1.0	28.1 28.1	28.1	8.5 8.5	8.5	18.0 18.0	18.0	118.3 117.3	117.8	8.4 8.3	8.3	8.3	7.9 7.7	7.8	7.8	4.3 5.7	5.0	5.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	1.9	27.3 27.6	27.5	8.4 8.4	8.4	20.6 19.8	20.2	112.7 108.5	110.6	8.0 7.7	7.8		7.8 7.8	7.8		5.8 5.1	5.5				
30-May-14	Sunny	Moderate	12:44	3.4	Surface	1.0	28.1 28.1	28.1	8.6 8.6	8.6	18.0 18.0	18.0	121.0 124.1	122.6	8.6 8.8	8.7	8.7	2.1 2.2	2.2	2.3	2.8 2.6	2.7	4.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.4	28.0 27.9	28.0	8.6 8.6	8.6	19.5 19.1	19.3	123.0 113.7	118.4	8.6 8.0	8.3		2.3 2.2	2.3		5.4 5.7	5.6				

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-May-14	Sunny	Moderate	08:24	3.5	Surface	1.0	23.9 23.9	23.9	8.4 8.4	8.4	26.4 26.4	26.4	88.4 88.2	88.3	6.4 6.4	6.4	6.4	5.6 5.7	5.7	5.8	4.7 5.4	5.1	5.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.5	23.9 23.9	23.9	8.4 8.4	8.4	26.5 26.5	26.5	88.6 88.3	88.5	6.4 6.4	6.4		5.9 5.7	5.8		6.4	5.9 5.7		5.8	4.9 5.6	5.3
5-May-14	Sunny	Moderate	09:59	3.1	Surface	1.0	24.1 24.1	24.1	8.4 8.4	8.4	26.4 26.5	26.5	97.0 97.9	97.5	7.0 7.1	7.0	7.0	2.2 2.3	2.3	2.4	2.6 2.5	2.6	2.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.1	24.1 24.1	24.1	8.4 8.4	8.4	26.6 26.5	26.5	98.8 97.3	98.1	7.1 7.0	7.1		2.6 2.4	2.5		7.1	2.6 2.4		2.5	3.3 2.2	2.8
7-May-14	Cloudy	Moderate	11:54	3.3	Surface	1.0	23.0 23.0	23.0	8.4 8.4	8.4	27.5 27.6	27.5	93.5 99.5	96.5	6.8 7.3	7.1	7.1	2.3 2.4	2.4	2.5	6.1 6.8	6.5	6.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	23.0 23.0	23.0	8.4 8.4	8.4	27.6 27.6	27.6	93.4 93.5	93.5	6.8 6.8	6.8		2.5 2.5	2.5		6.8	2.5 2.5		2.5	6.3 7.0	6.7
9-May-14	Rainy	Moderate	10:31	3.2	Surface	1.0	23.3 23.3	23.3	8.4 8.4	8.4	26.9 26.9	26.9	92.1 90.3	91.2	6.7 6.6	6.7	6.7	9.5 9.5	9.5	9.5	4.3 5.5	4.9	5.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	23.3 23.3	23.3	8.3 8.3	8.3	27.4 27.4	27.4	91.2 95.0	93.1	6.6 6.9	6.8		9.5 9.5	9.5		6.8	9.5 9.5		9.5	5.6 5.2	5.4
12-May-14	Sunny	Moderate	16:39	3.2	Surface	1.0	25.3 25.6	25.5	8.2 8.2	8.2	17.1 16.8	17.0	92.2 93.9	93.1	6.9 7.1	7.0	7.0	8.0 8.2	8.1	8.3	3.6 3.5	3.6	3.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	24.3 24.4	24.3	8.2 8.2	8.2	18.7 18.8	18.7	92.4 91.6	92.0	6.9 6.8	6.8		8.4 8.4	8.4		6.8	8.4 8.4		8.4	4.3 3.2	3.8
14-May-14	Sunny	Moderate	18:32	3.0	Surface	1.0	25.8 25.7	25.7	7.7 7.7	7.7	21.5 21.8	21.7	90.3 89.9	90.1	6.5 6.5	6.5	6.5	16.2 16.8	16.5	16.6	6.8 7.0	6.9	6.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.0	25.4 25.7	25.6	7.6 7.7	7.7	22.6 22.5	22.6	89.1 90.5	89.8	6.4 6.5	6.5		16.5 16.8	16.7		6.5	16.5 16.8		16.7	6.4 6.2	6.3
16-May-14	Cloudy	Moderate	07:45	3.1	Surface	1.0	25.7 25.7	25.7	7.6 7.6	7.6	18.1 18.0	18.0	83.9 84.0	84.0	6.2 6.2	6.2	6.2	4.9 4.7	4.8	4.8	4.3 4.8	4.6	4.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.1	25.7 25.7	25.7	7.6 7.6	7.6	18.0 18.2	18.1	84.1 83.9	84.0	6.2 6.2	6.2		4.8 4.8	4.8		6.2	4.8 4.8		4.8	5.7 4.3	5.0
19-May-14	Cloudy	Moderate	10:18	3.2	Surface	1.0	26.2 26.2	26.2	7.5 7.5	7.5	16.0 15.9	16.0	82.7 81.1	81.9	6.1 6.0	6.1	6.1	3.1 3.2	3.2	3.2	3.1 3.1	3.1	3.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	26.2 26.2	26.2	7.5 7.5	7.5	16.1 16.2	16.1	81.7 85.2	83.5	6.0 6.3	6.2		3.2 3.1	3.2		6.2	3.2 3.1		3.2	3.0 3.3	3.2
21-May-14	Cloudy	Moderate	12:02	3.2	Surface	1.0	26.4 26.4	26.4	7.6 7.6	7.6	14.9 14.9	14.9	91.1 91.2	91.2	6.8 6.8	6.8	6.8	2.6 2.8	2.7	2.7	2.2 3.8	3.0	3.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	26.4 26.4	26.4	7.6 7.6	7.6	15.8 15.8	15.8	91.6 91.4	91.5	6.8 6.7	6.7		2.7 2.6	2.7		6.7	2.7 2.6		2.7	4.0 3.5	3.8

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
23-May-14	Cloudy	Moderate	13:28	3.1	Surface	1.0	26.5 26.6	26.5	7.6 7.6	7.6	16.2 16.1	16.2	83.2 83.0	83.1	6.1 6.1	6.1	6.1	5.4 5.9	5.7	6.4	2.5 2.8	2.7	2.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.1	26.2 26.4	26.3	7.5 7.6	7.6	18.6 18.2	18.4	81.6 82.6	82.1	5.9 6.0	6.0		6.0	7.0 7.1		7.1	7.0		7.1	2.4 3.0	2.7
26-May-14	Sunny	Moderate	17:22	2.9	Surface	1.0	29.2 29.2	29.2	7.9 7.8	7.9	13.8 13.8	13.8	128.3 120.3	124.3	9.1 8.6	8.8	8.8	6.8 7.2	7.0	7.7	3.2 3.2	3.2	3.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	1.9	28.1 28.1	28.1	7.7 7.8	7.8	16.9 16.8	16.8	115.1 125.7	120.4	8.2 8.9	8.6		8.6	8.7 7.8		8.3	8.7		7.8	4.4 3.7	4.1
28-May-14	Sunny	Moderate	18:49	2.9	Surface	1.0	27.9 28.1	28.0	8.6 8.6	8.6	19.6 19.1	19.3	128.8 130.7	129.8	9.1 9.2	9.1	9.1	7.7 7.8	7.8	7.8	4.7 5.2	5.0	5.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	1.9	27.6 27.7	27.7	8.5 8.5	8.5	19.7 19.5	19.6	126.5 120.8	123.7	8.9 8.5	8.7		8.7	7.6 7.7		7.7	7.6		7.7	6.0 6.1	6.1
30-May-14	Sunny	Moderate	07:24	3.2	Surface	1.0	27.5 27.5	27.5	8.3 8.2	8.3	15.6 15.8	15.7	101.9 96.3	99.1	7.4 7.0	7.2	7.2	1.7 1.8	1.8	1.8	4.0 4.1	4.1	4.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.2	27.0 27.5	27.2	8.4 8.3	8.3	16.4 15.8	16.1	97.8 94.4	96.1	7.1 6.8	7.0		7.0	1.7 1.8		1.8	1.7		1.8	3.8 4.5	4.2

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)9 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-May-14	Sunny	Moderate	14:10	3.5	Surface	1.0	24.4 24.4	24.4	8.3 8.3	8.3	26.6 26.6	26.6	91.4 91.3	91.4	6.6 6.6	6.6	6.6	4.8 4.8	4.8	5.0	5.4 4.6	5.0	4.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		5.0	-		-	-	-
					Bottom	2.5	24.3 24.4	24.3	8.3 8.3	8.3	26.7 26.6	26.7	91.3 91.3	91.3	6.6 6.6	6.6		6.6	5.1 5.0		5.1	5.0		4.6 3.8	4.2	
5-May-14	Sunny	Moderate	16:06	3.4	Surface	1.0	24.3 24.3	24.3	8.4 8.4	8.4	26.3 26.2	26.3	98.0 99.8	98.9	7.1 7.2	7.1	7.1	2.5 2.7	2.6	2.8	3.2 2.1	2.7	3.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.4	24.3 24.3	24.3	8.4 8.4	8.4	27.4 27.3	27.4	98.6 100.5	99.6	7.1 7.2	7.1		7.1	2.8 3.0		2.9	2.9		4.8 4.6	4.7	
7-May-14	Cloudy	Moderate	17:40	3.4	Surface	1.0	23.4 23.5	23.4	8.4 8.4	8.4	28.5 28.6	28.6	98.8 93.3	96.1	7.1 6.7	6.9	6.9	6.7 6.8	6.8	6.9	6.8 6.0	6.4	6.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.4	23.4 23.4	23.4	8.4 8.4	8.4	29.0 28.8	28.9	94.3 91.1	92.7	6.8 6.6	6.7		6.7	7.0 7.0		7.0	7.0		6.3 5.2	5.8	
9-May-14	Rainy	Moderate	14:13	3.8	Surface	1.0	23.3 23.3	23.3	8.4 8.4	8.4	27.8 27.8	27.8	90.9 91.4	91.2	6.6 6.6	6.6	6.6	10.6 10.2	10.4	10.3	10.2 9.6	9.9	10.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.8	23.3 23.4	23.4	8.3 8.4	8.3	27.9 27.8	27.9	92.5 91.1	91.8	6.7 6.6	6.7		6.7	10.2 10.2		10.2	10.2		11.0 10.2	10.6	
12-May-14	Sunny	Moderate	12:09	3.5	Surface	1.0	24.0 24.0	24.0	8.2 8.2	8.2	17.4 17.4	17.4	90.9 91.7	91.3	6.9 7.0	6.9	6.9	9.0 9.1	9.1	9.2	4.2 3.1	3.7	4.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.5	24.0 24.1	24.0	8.1 8.2	8.2	18.4 20.1	19.3	91.1 90.6	90.9	7.0 6.8	6.9		6.9	9.3 9.2		9.3	9.3		6.0 5.6	5.8	
14-May-14	Sunny	Moderate	13:32	3.6	Surface	1.0	25.3 25.3	25.3	7.7 7.6	7.7	20.2 20.2	20.2	88.1 88.8	88.5	6.5 6.5	6.5	6.5	19.8 19.2	19.5	19.5	8.4 7.7	8.1	8.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.6	25.2 25.2	25.2	7.7 7.6	7.6	20.5 20.6	20.6	88.0 90.1	89.1	6.5 6.6	6.5		6.5	19.8 19.1		19.5	19.5		7.6 8.3	8.0	
16-May-14	Cloudy	Moderate	13:22	3.7	Surface	1.0	26.0 26.1	26.0	7.6 7.6	7.6	18.0 18.0	18.0	88.2 88.8	88.5	6.5 6.5	6.5	6.5	4.7 5.0	4.9	5.1	4.3 2.9	3.6	4.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.7	25.8 25.9	25.9	7.5 7.6	7.6	19.5 19.4	19.5	90.0 88.5	89.3	6.6 6.5	6.5		6.5	5.3 5.3		5.3	5.3		4.6 4.6	4.6	
19-May-14	Sunny	Rough	15:30	3.7	Surface	1.0	26.8 26.8	26.8	7.5 7.5	7.5	16.0 16.1	16.1	90.6 90.0	90.3	6.6 6.6	6.6	6.6	4.1 4.3	4.2	4.2	4.6 5.2	4.9	7.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.7	26.8 26.8	26.8	7.4 7.5	7.5	16.1 16.2	16.1	91.7 90.0	90.9	6.7 6.6	6.6		6.6	4.2 4.1		4.2	4.2		9.6 10.2	9.9	
21-May-14	Cloudy	Moderate	17:31	3.6	Surface	1.0	26.8 26.9	26.9	7.6 7.6	7.6	15.6 15.6	15.6	90.4 91.5	91.0	6.6 6.7	6.7	6.7	4.7 4.7	4.7	4.8	5.9 5.2	5.6	6.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-		
					Bottom	2.6	26.7 26.8	26.8	7.5 7.6	7.5	17.1 16.9	17.0	94.0 91.7	92.9	6.8 6.7	6.8		6.8	4.7 4.8		4.8	4.8		5.6 6.9	6.3	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)9 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)			Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	09:35	3.4	Surface	1.0	<u>26.5</u> 26.5	26.5	<u>7.7</u> 7.7	7.7	15.4 <u>15.6</u>	15.5	85.8 <u>86.5</u>	86.2	6.3 6.4	6.3	6.3	5.4 <u>5.7</u>	5.6	7.4	3.2 <u>3.2</u>	3.2	5.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.4	<u>26.5</u> 26.5	26.5	<u>7.6</u> 7.6	7.6	16.5 <u>16.3</u>	16.4	87.3 <u>85.9</u>	86.6	6.4 6.3	6.3		6.3	9.0 <u>9.2</u>		9.1	6.8 <u>7.4</u>		7.1	6.8 <u>7.4</u>	7.1	
26-May-14	Sunny	Moderate	12:13	3.5	Surface	1.0	<u>27.6</u> 27.8	27.7	<u>7.6</u> 7.5	7.6	14.0 <u>13.9</u>	13.9	92.1 <u>93.8</u>	93.0	6.7 6.8	6.8	6.8	5.3 <u>5.0</u>	5.2	5.8	2.0 <u>2.3</u>	2.2	2.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.5	<u>27.5</u> 27.2	27.3	<u>7.5</u> 7.4	7.5	17.4 <u>17.4</u>	17.4	92.8 <u>92.2</u>	92.5	6.7 6.6	6.7		6.7	6.3 <u>6.3</u>		6.3	3.3 <u>3.3</u>		3.3	3.3 <u>3.3</u>	3.3	
28-May-14	Sunny	Moderate	13:21	3.8	Surface	1.0	<u>28.6</u> 28.4	28.5	<u>8.5</u> 8.5	8.5	17.1 <u>17.3</u>	17.2	121.4 <u>118.9</u>	120.2	8.6 8.4	8.5	8.5	20.5 <u>20.2</u>	20.4	20.7	5.5 <u>4.5</u>	5.0	5.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.8	<u>28.4</u> <u>28.2</u>	28.3	<u>8.5</u> <u>8.5</u>	8.5	17.4 <u>17.9</u>	17.6	119.4 <u>119.4</u>	119.4	8.4 8.4	8.4		8.4	20.8 <u>21.1</u>		21.0	4.9 <u>5.3</u>		5.1	5.3 <u>5.3</u>	5.1	
30-May-14	Sunny	Moderate	12:57	3.6	Surface	1.0	<u>28.0</u> 27.9	28.0	<u>8.5</u> 8.5	8.5	18.1 <u>18.1</u>	18.1	119.9 <u>123.1</u>	121.5	8.5 8.7	8.6	8.6	5.5 <u>5.4</u>	5.5	5.5	6.3 <u>4.2</u>	5.3	5.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	<u>27.9</u> <u>28.2</u>	28.1	<u>8.5</u> <u>8.5</u>	8.5	19.5 <u>19.2</u>	19.4	121.5 <u>107.9</u>	114.7	8.5 7.6	8.1		8.1	5.5 <u>5.5</u>		5.5	5.8 <u>5.9</u>		5.9	5.9 <u>5.9</u>	5.9	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)9 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-May-14	Sunny	Moderate	08:12	3.5	Surface	1.0	23.9 23.9	23.9	8.4 8.4	8.4	26.5 26.5	26.5	87.8 88.0	87.9	6.4 6.4	6.4	6.4	3.4 3.6	3.5	3.7	3.5 3.8	3.7	3.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.5	23.9 23.9	23.9	8.4 8.4	8.4	26.6 26.6	26.6	87.8 87.9	87.9	6.4 6.4	6.4		6.4	3.8 3.9		3.9	6.4		3.8 3.9	3.9	3.2 3.6	3.6
5-May-14	Sunny	Moderate	09:45	3.6	Surface	1.0	24.2 24.2	24.2	8.4 8.4	8.4	26.4 26.3	26.4	96.9 95.5	96.2	7.0 6.9	6.9	6.9	2.1 2.0	2.1	2.1	3.3 2.4	2.9	3.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	24.2 24.2	24.2	8.4 8.4	8.4	26.6 26.6	26.6	98.1 95.8	97.0	7.1 6.9	7.0		7.0	2.0 2.0		2.0	7.0		2.0 2.0	2.0	3.2 4.4	3.8
7-May-14	Cloudy	Moderate	11:40	3.4	Surface	1.0	23.4 23.4	23.4	8.4 8.4	8.4	28.5 28.4	28.5	93.3 99.5	96.4	6.7 7.2	7.0	7.0	5.0 5.0	5.0	5.2	4.9 5.2	5.1	5.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.4	23.4 23.3	23.4	8.4 8.4	8.4	28.6 28.7	28.7	92.1 95.1	93.6	6.7 6.9	6.8		6.8	5.2 5.3		5.3	6.8		5.2 5.3	5.3	5.6 4.6	5.1
9-May-14	Rainy	Moderate	10:19	3.7	Surface	1.0	23.3 23.3	23.3	8.4 8.4	8.4	28.0 28.0	28.0	93.6 92.7	93.2	6.8 6.7	6.8	6.8	8.4 8.5	8.5	8.5	13.8 13.7	13.8	14.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	23.3 23.3	23.3	8.3 8.4	8.3	28.0 28.0	28.0	95.0 93.0	94.0	6.9 6.8	6.8		6.8	8.6 8.3		8.5	6.8		8.6 8.3	8.5	15.0 14.6	14.8
12-May-14	Sunny	Moderate	16:53	3.8	Surface	1.0	24.4 24.8	24.6	8.2 8.2	8.2	18.6 18.5	18.6	91.5 92.9	92.2	6.8 6.9	6.9	6.9	12.2 12.0	12.1	12.3	4.3 3.4	3.9	4.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.8	24.9 24.7	24.8	8.2 8.2	8.2	20.0 19.3	19.6	91.9 90.8	91.4	6.9 6.8	6.8		6.8	12.6 12.4		12.5	6.8		12.6 12.4	12.5	4.4 5.4	4.9
14-May-14	Sunny	Moderate	18:46	3.7	Surface	1.0	25.3 25.3	25.3	7.6 7.6	7.6	21.7 21.7	21.7	88.8 87.4	88.1	6.5 6.4	6.4	6.4	15.2 15.1	15.2	16.0	5.7 6.4	6.1	5.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	25.1 25.0	25.1	7.5 7.6	7.6	22.0 22.1	22.1	90.5 86.7	88.6	6.6 6.3	6.5		6.5	16.7 16.9		16.8	6.5		16.7 16.9	16.8	5.8 5.6	5.7
16-May-14	Cloudy	Moderate	07:32	3.6	Surface	1.0	25.7 25.7	25.7	7.7 7.7	7.7	18.1 18.0	18.1	87.5 86.1	86.8	6.4 6.3	6.4	6.4	5.4 5.4	5.4	5.5	6.8 5.8	6.3	6.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	25.9 25.8	25.8	7.7 7.7	7.7	19.1 19.2	19.2	89.1 86.9	88.0	6.5 6.4	6.4		6.4	5.6 5.6		5.6	6.4		5.6 5.6	5.6	6.4 4.8	5.6
19-May-14	Cloudy	Moderate	10:01	4.1	Surface	1.0	26.2 26.2	26.2	7.6 7.6	7.6	15.5 15.8	15.6	84.4 85.6	85.0	6.3 6.3	6.3	6.3	4.4 4.2	4.3	4.4	3.2 4.5	3.9	4.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	26.3 26.3	26.3	7.6 7.6	7.6	17.1 17.1	17.1	85.4 87.6	86.5	6.3 6.4	6.3		6.3	4.3 4.4		4.4	6.3		4.3 4.4	4.4	5.2 4.9	5.1
21-May-14	Cloudy	Moderate	11:48	3.6	Surface	1.0	26.4 26.4	26.4	7.6 7.6	7.6	15.3 15.4	15.3	87.1 88.1	87.6	6.4 6.5	6.5	6.5	5.9 5.9	5.9	6.1	5.6 5.6	5.6	5.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	26.4 26.4	26.4	7.6 7.6	7.6	15.5 15.5	15.5	89.8 87.3	88.6	6.6 6.4	6.5		6.5	6.2 6.2		6.2	6.5		6.2 6.2	6.2	6.0 6.1	6.1

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)9 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	13:42	3.2	Surface	1.0	<u>26.4</u> 26.4	26.4	<u>7.7</u> 7.6	7.6	15.7 15.7	15.7	90.1 91.1	90.6	6.6 6.7	6.7	6.7	3.2 3.1	3.2	3.4	2.9 3.2	3.1	3.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.2	<u>26.4</u> 26.4	26.4	<u>7.6</u> 7.6	7.6	15.8 15.9	15.8	89.2 91.3	90.3	6.6 6.7	6.6		6.6	3.7 3.4		3.6	6.6		3.7 3.4	3.6	6.6	3.4 2.6
26-May-14	Sunny	Moderate	17:37	3.3	Surface	1.0	<u>28.5</u> 28.6	28.6	<u>7.8</u> 7.8	7.8	14.3 14.3	14.3	109.2 114.3	111.8	7.8 8.2	8.0	8.0	8.6 7.9	8.3	9.8	2.8 3.0	2.9	2.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.3	<u>28.2</u> 28.0	28.1	<u>7.7</u> 7.7	7.7	16.3 17.1	16.7	111.6 105.5	108.6	8.0 7.5	7.7		7.7	11.0 11.6		11.3	7.7		11.0 11.6	11.3	7.7	2.8 2.8
28-May-14	Sunny	Moderate	19:01	3.6	Surface	1.0	<u>29.1</u> 29.0	29.1	<u>8.6</u> 8.7	8.6	17.1 17.1	17.1	150.3 156.6	153.5	10.5 11.0	10.7	10.7	9.3 9.7	9.5	9.5	9.4 8.1	8.8	8.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	<u>28.8</u> 26.9	27.9	<u>8.7</u> 8.6	8.6	18.3 21.5	19.9	148.3 148.9	148.6	10.3 10.4	10.3		10.3	9.6 9.4		9.5	10.3		9.6 9.4	9.5	10.3	7.9 8.1
30-May-14	Sunny	Moderate	07:11	3.6	Surface	1.0	<u>27.7</u> 27.7	27.7	<u>8.5</u> 8.4	8.4	16.7 16.8	16.8	111.3 109.1	110.2	8.0 7.8	7.9	7.9	1.7 1.8	1.8	1.8	5.4 4.3	4.9	5.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	<u>27.6</u> 27.7	27.7	<u>8.3</u> 8.5	8.4	17.7 17.4	17.5	104.5 111.0	107.8	7.5 7.9	7.7		7.7	1.8 1.8		1.8	7.7		1.8 1.8	1.8	7.7	6.6 6.2

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS10 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	15:00	10.9	Surface	1.0	24.3 24.3	24.3	8.2 8.2	8.2	26.9 26.9	26.9	89.8 90.0	89.9	6.5 6.5	6.5	6.5	3.7 3.8	3.8	3.8	3.8 3.4	3.6	4.3
					Middle	5.5	24.2 24.1	24.2	8.2 8.2	8.2	27.2 27.3	27.3	89.7 90.0	89.9	6.5 6.5	6.5		3.7 3.7	3.7		5.1 4.6	4.9	
					Bottom	9.9	23.9 24.1	24.0	8.2 8.2	8.2	29.2 28.7	29.0	89.1 89.1	89.1	6.4 6.4	6.4		3.8 3.9	3.9		5.2 3.7	4.5	
5-May-14	Sunny	Moderate	17:00	10.5	Surface	1.0	24.3 24.3	24.3	8.3 8.3	8.3	26.1 26.0	26.0	88.9 89.5	89.2	6.4 6.5	6.4	6.4	2.5 2.6	2.6	3.2	2.9 2.1	2.5	2.9
					Middle	5.3	24.2 24.1	24.1	8.3 8.3	8.3	28.6 28.7	28.7	87.8 87.8	87.8	6.3 6.3	6.3		3.4 3.5	3.5		4.2 2.1	3.2	
					Bottom	9.5	24.0 23.9	24.0	8.2 8.2	8.2	30.1 30.3	30.2	88.2 88.4	88.3	6.3 6.3	6.3		3.3 3.4	3.4		3.5 2.7	3.1	
7-May-14	Cloudy	Moderate	18:47	10.4	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	29.9 29.9	29.9	89.4 88.7	89.1	6.4 6.3	6.4	6.4	3.0 3.2	3.1	3.5	5.2 4.8	5.0	5.7
					Middle	5.2	23.7 23.7	23.7	8.2 8.2	8.2	30.1 30.2	30.2	88.0 87.9	88.0	6.3 6.3	6.3		3.7 3.7	3.7		6.5 6.0	6.3	
					Bottom	9.4	23.7 23.7	23.7	8.2 8.2	8.2	30.9 30.7	30.8	88.2 88.5	88.4	6.3 6.3	6.3		3.8 3.7	3.8		6.6 5.1	5.9	
9-May-14	Rainy	Moderate	09:50	10.4	Surface	1.0	23.6 23.6	23.6	8.2 8.1	8.2	28.0 28.0	28.0	87.2 88.2	87.7	6.3 6.4	6.3	6.2	4.0 3.8	3.9	6.6	5.1 5.6	5.4	5.5
					Middle	5.2	23.7 23.6	23.7	8.1 8.2	8.1	30.3 30.3	30.3	85.6 85.6	85.6	6.1 6.1	6.1		8.3 7.9	8.1		6.3 5.3	5.8	
					Bottom	9.4	23.6 23.6	23.6	8.1 8.1	8.1	30.4 30.3	30.4	86.1 86.4	86.3	6.1 6.2	6.1		7.8 7.6	7.7		5.1 5.2	5.2	
12-May-14	Sunny	Moderate	11:32	10.6	Surface	1.0	24.1 24.1	24.1	8.0 8.0	8.0	13.8 14.1	14.0	84.5 83.5	84.0	6.6 6.5	6.5	6.4	9.1 9.2	9.2	12.4	3.9 3.1	3.5	3.9
					Middle	5.3	23.7 23.7	23.7	7.8 8.0	7.9	21.2 20.3	20.7	82.2 81.9	82.1	6.2 6.2	6.2		13.5 13.4	13.5		5.2 3.1	4.2	
					Bottom	9.6	23.7 23.7	23.7	7.6 7.9	7.8	24.5 24.8	24.6	83.6 82.9	83.3	6.2 6.1	6.1		14.5 14.6	14.6		4.5 3.7	4.1	
14-May-14	Sunny	Moderate	12:41	10.1	Surface	1.0	25.2 25.2	25.2	8.1 8.1	8.1	17.9 17.9	17.9	86.9 85.9	86.4	6.5 6.4	6.4	6.4	6.6 6.2	6.4	10.3	6.1 6.1	6.1	7.1
					Middle	5.1	25.0 24.9	25.0	8.1 8.1	8.1	19.9 20.4	20.1	85.2 86.8	86.0	6.3 6.4	6.3		10.8 11.1	11.0		7.6 5.9	6.8	
					Bottom	9.1	24.8 24.9	24.9	8.1 8.1	8.1	21.3 21.4	21.4	87.6 85.4	86.5	6.4 6.3	6.4		13.3 13.5	13.4		8.5 8.3	8.4	
16-May-14	Cloudy	Moderate	13:48	11.3	Surface	1.0	25.4 25.3	25.4	8.1 8.1	8.1	17.8 19.1	18.5	81.7 81.6	81.7	6.1 6.0	6.0	6.0	7.7 7.9	7.8	8.8	4.5 4.6	4.6	5.0
					Middle	5.7	25.3 25.3	25.3	8.1 8.1	8.1	19.9 20.5	20.2	81.4 81.5	81.5	6.0 6.0	6.0		9.0 9.0	9.0		4.7 4.6	4.7	
					Bottom	10.3	25.3 25.3	25.3	8.1 8.1	8.1	21.2 21.4	21.3	81.3 81.7	81.5	5.9 6.0	5.9		9.4 9.5	9.5		5.2 6.0	5.6	
19-May-14	Sunny	Rough	16:47	11.1	Surface	1.0	26.8 26.7	26.7	8.1 8.1	8.1	14.3 14.4	14.4	80.5 79.9	80.2	5.9 5.9	5.9	5.8	4.2 4.3	4.3	4.4	3.2 3.3	3.3	3.5
					Middle	5.6	25.7 26.1	25.9	8.0 8.1	8.0	17.6 15.2	16.4	78.1 77.0	77.6	5.7 5.7	5.7		4.4 4.4	4.4		3.3 3.2	3.3	
					Bottom	10.1	25.8 25.7	25.7	8.0 8.0	8.0	19.7 19.9	19.8	77.2 76.3	76.8	5.7 5.6	5.7		4.5 4.6	4.6		3.4 4.1	3.8	
21-May-14	Cloudy	Moderate	18:14	10.2	Surface	1.0	26.2 26.3	26.2	8.1 8.1	8.1	14.2 15.2	14.7	72.6 73.7	73.2	5.4 5.5	5.4	5.3	4.0 3.6	3.8	4.1	7.3 6.4	6.9	6.8
					Middle	5.1	25.7 25.7	25.7	8.1 8.1	8.1	20.3 20.3	20.3	71.4 71.8	71.6	5.2 5.2	5.2		4.5 4.3	4.4		7.1 7.5	7.3	
					Bottom	9.2	25.7 25.7	25.7	8.0 8.0	8.0	20.9 20.5	20.7	72.9 71.9	72.4	5.3 5.2	5.3		3.9 4.1	4.0		6.0 6.2	6.1	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS10 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	09:08	10.4	Surface	1.0	26.2 26.2	26.2	8.1 8.1	8.1	13.9 14.1	14.0	70.0 71.9	71.0	5.2 5.4	5.3	5.3	4.9 5.0	5.0	6.2	4.0 2.9	3.5	3.5
					Middle	5.2	25.8 25.8	25.8	8.1 8.1	8.1	18.7 18.2	18.5	69.3 71.4	70.4	5.1 5.3	5.2		6.7 6.9	6.8		3.3 4.3	3.8	
					Bottom	9.4	25.5 25.1	25.3	7.9 8.1	8.0	26.3 26.3	26.3	70.5 73.5	72.0	5.0 5.2	5.1		6.5 6.8	6.7		3.6 2.7	3.2	
26-May-14	Sunny	Moderate	11:50	10.5	Surface	1.0	27.0 27.1	27.1	7.9 8.0	8.0	11.9 11.0	11.4	70.0 70.6	70.3	5.2 5.3	5.3	5.2	6.5 6.3	6.4	6.7	3.9 3.3	3.6	4.8
					Middle	5.3	26.5 26.5	26.5	8.0 8.0	8.0	14.4 14.5	14.5	67.5 68.0	67.8	5.0 5.0	5.0		6.4 6.6	6.5		5.3 5.3	5.3	
					Bottom	9.5	25.9 26.0	25.9	8.0 7.8	7.9	21.2 21.2	21.2	69.9 67.1	68.5	5.1 4.8	4.9		7.1 7.4	7.3		5.5 5.5	5.5	
28-May-14	Sunny	Moderate	12:32	11.1	Surface	1.0	27.6 27.2	27.4	8.1 8.1	8.1	15.4 15.7	15.5	85.6 85.6	85.6	6.2 6.1	6.2	6.1	2.1 2.0	2.1	2.2	4.2 3.2	3.7	3.3
					Middle	5.6	26.9 27.0	27.0	8.1 8.1	8.1	17.2 17.8	17.5	81.8 83.3	82.6	5.9 6.0	5.9		2.1 2.2	2.2		4.3 2.6	3.5	
					Bottom	10.1	26.8 27.2	27.0	8.1 8.1	8.1	18.8 18.5	18.7	80.4 82.6	81.5	5.8 6.0	5.9		2.4 2.4	2.4		2.1 3.0	2.6	
30-May-14	Sunny	Moderate	13:57	10.4	Surface	1.0	27.6 27.6	27.6	8.1 8.1	8.1	14.6 14.7	14.6	82.5 79.0	80.8	6.0 5.7	5.9	5.6	2.9 2.8	2.9	4.7	2.9 2.6	2.8	2.9
					Middle	5.2	26.7 26.7	26.7	8.1 8.1	8.1	19.8 20.2	20.0	74.2 72.4	73.3	5.3 5.2	5.3		5.4 5.6	5.5		2.8 2.5	2.7	
					Bottom	9.4	26.5 26.5	26.5	8.0 8.0	8.0	23.6 23.0	23.3	74.6 77.2	75.9	5.3 5.5	5.4		5.6 5.5	5.6		2.5 4.0	3.3	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS10 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	08:02	10.6	Surface	1.0	23.9 23.9	23.9	8.2 8.1	8.2	27.5 27.1	27.3	85.2 86.4	85.8	6.1 6.2	6.2	6.2	4.9 4.8	4.9	8.5	5.1 4.5	4.8	5.6
					Middle	5.3	23.8 23.9	23.9	8.2 8.2	8.2	27.9 27.8	27.9	85.0 86.3	85.7	6.1 6.2	6.2		10.1 10.4	10.3		5.5 6.2	5.9	
					Bottom	9.6	23.8 23.9	23.9	8.2 8.2	8.2	28.0 27.9	27.9	85.1 86.8	86.0	6.1 6.2	6.2		10.4 10.3	10.4		6.4 5.5	6.0	
5-May-14	Sunny	Moderate	09:37	10.7	Surface	1.0	24.3 24.3	24.3	8.2 8.2	8.2	22.2 22.1	22.2	89.5 87.9	88.7	6.6 6.5	6.5	6.4	4.4 4.4	4.4	5.2	4.2 3.7	4.0	3.6
					Middle	5.4	24.0 24.0	24.0	8.2 8.2	8.2	29.1 29.1	29.1	89.8 87.1	88.5	6.4 6.2	6.3		5.2 5.5	5.4		2.7 3.4	3.1	
					Bottom	9.7	24.1 24.0	24.0	8.2 8.2	8.2	29.3 29.3	29.3	87.9 92.0	90.0	6.3 6.5	6.4		5.7 5.6	5.7		3.3 3.9	3.6	
7-May-14	Cloudy	Moderate	11:25	10.8	Surface	1.0	23.7 23.7	23.7	8.2 8.2	8.2	30.2 30.1	30.1	89.1 88.0	88.6	6.3 6.3	6.3	6.3	5.1 4.9	5.0	5.7	6.5 5.9	6.2	7.0
					Middle	5.4	23.8 23.7	23.8	8.2 8.2	8.2	30.7 30.6	30.6	89.5 87.6	88.6	6.4 6.2	6.3		5.7 5.2	5.5		6.9 7.6	7.3	
					Bottom	9.8	23.8 23.8	23.8	8.2 8.2	8.2	30.9 30.9	30.9	88.1 91.9	90.0	6.2 6.5	6.4		6.4 6.6	6.5		8.2 6.9	7.6	
9-May-14	Rainy	Moderate	14:46	10.3	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	28.5 28.4	28.5	86.9 87.2	87.1	6.3 6.3	6.3	6.2	4.9 4.2	4.6	6.9	5.0 4.9	5.0	5.5
					Middle	5.2	23.7 23.7	23.7	8.2 8.2	8.2	30.6 30.6	30.6	84.8 85.5	85.2	6.0 6.1	6.0		8.8 8.6	8.7		5.1 5.6	5.4	
					Bottom	9.3	23.7 23.7	23.7	8.2 8.2	8.2	30.6 30.6	30.6	86.6 86.3	86.5	6.2 6.1	6.1		7.3 7.4	7.4		5.8 6.2	6.0	
12-May-14	Sunny	Moderate	17:47	10.7	Surface	1.0	24.4 24.3	24.4	8.1 8.1	8.1	14.7 15.0	14.9	83.3 83.0	83.2	6.4 6.4	6.4	6.3	9.3 9.2	9.3	10.5	5.2 4.7	5.0	4.6
					Middle	5.4	23.9 23.8	23.9	8.1 8.1	8.1	19.5 20.7	20.1	80.7 80.5	80.6	6.1 6.0	6.1		10.8 10.6	10.7		3.7 4.4	4.1	
					Bottom	9.7	23.7 23.7	23.7	8.0 8.0	8.0	26.5 26.7	26.6	80.7 79.7	80.2	5.9 5.8	5.8		11.5 11.5	11.5		4.5 4.9	4.7	
14-May-14	Sunny	Moderate	19:23	10.2	Surface	1.0	25.8 25.8	25.8	8.0 8.0	8.0	14.5 13.5	14.0	84.2 84.5	84.4	6.3 6.4	6.4	6.3	8.6 8.4	8.5	9.8	4.9 4.5	4.7	4.7
					Middle	5.1	25.2 24.9	25.1	8.0 8.0	8.0	18.9 19.7	19.3	83.1 81.5	82.3	6.1 6.0	6.1		10.9 11.3	11.1		3.9 5.1	4.5	
					Bottom	9.2	25.3 24.9	25.1	7.9 8.0	8.0	19.8 20.7	20.2	83.3 82.3	82.8	6.1 6.1	6.1		9.6 10.1	9.9		5.0 5.0	5.0	
16-May-14	Cloudy	Moderate	08:06	11.6	Surface	1.0	25.3 25.3	25.3	8.0 8.0	8.0	19.6 19.6	19.6	79.9 79.5	79.7	5.9 5.9	5.9	5.9	13.3 13.2	13.3	14.1	7.8 8.1	8.0	7.1
					Middle	5.8	25.1 25.2	25.1	8.1 8.1	8.1	20.4 19.8	20.1	80.1 79.4	79.8	5.9 5.8	5.9		14.3 14.5	14.4		7.8 6.6	7.2	
					Bottom	10.6	25.0 25.1	25.1	8.1 8.0	8.0	22.2 21.6	21.9	80.4 79.4	79.9	5.9 5.8	5.8		14.4 14.6	14.5		6.4 5.9	6.2	
19-May-14	Cloudy	Moderate	09:39	11.1	Surface	1.0	26.0 25.9	26.0	8.0 8.0	8.0	14.9 15.0	15.0	80.1 76.8	78.5	5.8 5.7	5.8	5.8	4.0 4.0	4.0	4.2	6.4 6.2	6.3	6.5
					Middle	5.6	25.8 25.6	25.7	8.0 8.0	8.0	15.1 16.2	15.7	76.6 79.0	77.8	5.7 5.9	5.8		4.1 4.2	4.2		6.0 6.1	6.1	
					Bottom	10.1	25.6 25.6	25.6	8.0 8.0	8.0	20.6 21.0	20.8	76.6 78.2	77.4	5.6 5.8	5.7		4.4 4.2	4.3		7.2 7.1	7.2	
21-May-14	Cloudy	Moderate	11:41	10.3	Surface	1.0	26.1 26.1	26.1	8.1 8.1	8.1	14.5 14.2	14.3	79.3 78.2	78.8	5.9 5.8	5.9	5.8	7.1 6.7	6.9	12.2	4.2 4.5	4.4	5.0
					Middle	5.2	25.6 25.8	25.7	8.1 8.1	8.1	22.2 19.3	20.8	77.8 76.0	76.9	5.6 5.6	5.6		12.7 13.1	12.9		5.0 5.5	5.3	
					Bottom	9.3	25.5 25.5	25.5	8.1 8.0	8.0	22.9 23.1	23.0	80.2 77.0	78.6	5.8 5.5	5.7		16.8 16.7	16.8		5.0 5.3	5.2	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS10 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	14:32	10.8	Surface	1.0	26.4 26.4	26.4	8.0 8.1	8.0	12.2 12.3	12.3	76.7 74.8	75.8	5.8 5.6	5.7	5.4	5.2 5.3	5.3	5.4	4.8 4.9	4.9	4.7
					Middle	5.4	25.8 25.7	25.8	8.0 8.0	8.0	18.1 19.3	18.7	70.0 69.7	69.9	5.2 5.1	5.1		5.5 5.2	5.4		5.3 3.8	4.6	
					Bottom	9.8	25.1 25.2	25.2	7.9 7.9	7.9	27.5 27.3	27.4	71.4 71.8	71.6	5.0 5.1	5.1		5.5 5.4	5.5		4.4 4.7	4.6	
26-May-14	Sunny	Moderate	17:50	10.9	Surface	1.0	27.7 27.8	27.7	8.1 8.0	8.1	9.7 9.8	9.8	80.7 81.3	81.0	6.0 6.1	6.0	5.8	6.4 6.3	6.4	7.9	5.2 5.0	5.1	5.7
					Middle	5.5	27.1 27.4	27.2	8.0 8.1	8.0	16.8 16.8	16.8	77.2 74.3	75.8	5.6 5.4	5.5		8.6 8.4	8.5		5.7 5.8	5.8	
					Bottom	9.9	25.7 25.8	25.7	7.9 7.9	7.9	25.1 24.4	24.8	72.2 76.1	74.2	5.1 5.4	5.3		8.7 8.8	8.8		6.2 6.2	6.2	
28-May-14	Sunny	Moderate	18:59	11.2	Surface	1.0	27.8 27.8	27.8	8.1 8.1	8.1	10.9 10.5	10.7	89.4 89.6	89.5	6.6 6.6	6.6	6.6	4.4 4.4	4.4	4.5	4.8 3.2	4.0	4.3
					Middle	5.6	27.7 27.7	27.7	8.1 8.1	8.1	12.8 12.4	12.6	89.3 89.4	89.4	6.5 6.5	6.5		4.4 4.4	4.4		4.5 5.5	5.0	
					Bottom	10.2	27.8 27.7	27.7	8.0 8.0	8.0	15.3 15.5	15.4	89.1 89.1	89.1	6.5 6.5	6.5		4.8 4.4	4.6		4.0 3.7	3.9	
30-May-14	Sunny	Moderate	06:57	10.9	Surface	1.0	27.2 27.1	27.1	8.1 8.1	8.1	18.1 18.5	18.3	79.1 76.3	77.7	5.7 5.5	5.6	5.4	5.3 5.5	5.4	5.6	4.7 4.6	4.7	5.2
					Middle	5.5	26.5 26.5	26.5	8.1 8.1	8.1	22.0 23.1	22.6	73.7 72.2	73.0	5.2 5.1	5.2		5.5 5.6	5.6		6.0 4.2	5.1	
					Bottom	9.9	26.4 26.3	26.3	8.1 8.1	8.1	24.1 24.4	24.3	74.4 75.1	74.8	5.2 5.3	5.3		5.6 5.7	5.7		5.8 5.6	5.7	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)11 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	15:09	10.4	Surface	1.0	24.1 24.2	24.1	8.2 8.2	8.2	27.1 27.3	27.2	90.4 89.0	89.7	6.5 6.4	6.5	6.5	7.7 7.5	7.6	9.4	4.7 4.5	4.6	4.7
					Middle	5.2	23.8 23.9	23.9	8.2 8.2	8.2	29.0 28.5	28.8	89.4 90.5	90.0	6.4 6.5	6.4		10.3 10.3	10.3		5.3 5.0	5.2	
					Bottom	9.4	24.0 23.9	23.9	8.2 8.2	8.2	28.8 29.2	29.0	93.2 88.9	91.1	6.7 6.4	6.5		10.4 10.2	10.3		5.2 3.4	4.3	
5-May-14	Sunny	Moderate	17:12	10.2	Surface	1.0	24.2 24.2	24.2	8.2 8.2	8.2	26.4 26.4	26.4	89.4 91.6	90.5	6.5 6.6	6.5	6.5	2.2 2.2	2.2	2.7	2.5 3.3	2.9	3.3
					Middle	5.1	24.0 24.0	24.0	8.2 8.2	8.2	29.0 29.0	29.0	89.1 92.2	90.7	6.4 6.6	6.5		2.9 3.0	3.0		3.4 4.1	3.8	
					Bottom	9.2	24.0 24.0	24.0	8.2 8.2	8.2	29.3 29.0	29.2	90.2 95.2	92.7	6.4 6.8	6.6		2.8 2.9	2.9		2.7 3.6	3.2	
7-May-14	Cloudy	Moderate	19:00	10.3	Surface	1.0	23.6 23.7	23.7	8.2 8.2	8.2	30.2 30.3	30.2	87.2 88.0	87.6	6.2 6.3	6.2	6.2	6.2 6.0	6.1	7.0	6.1 5.9	6.0	6.1
					Middle	5.2	23.7 23.7	23.7	8.2 8.2	8.2	30.9 30.7	30.8	88.5 84.9	86.7	6.3 6.0	6.2		7.4 7.4	7.4		6.6 6.4	6.5	
					Bottom	9.3	23.7 23.7	23.7	8.2 8.2	8.2	31.3 31.4	31.3	91.6 85.7	88.7	6.5 6.1	6.3		7.6 7.6	7.6		6.6 4.8	5.7	
9-May-14	Rainy	Moderate	09:38	10.2	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	28.7 28.6	28.7	86.8 86.3	86.6	6.3 6.2	6.2	6.2	4.6 4.9	4.8	5.7	5.9 5.8	5.9	6.5
					Middle	5.1	23.6 23.6	23.6	8.1 8.2	8.2	30.4 30.4	30.4	85.1 85.7	85.4	6.1 6.1	6.1		6.1 5.8	6.0		6.8 6.3	6.6	
					Bottom	9.2	23.6 23.7	23.7	8.2 8.1	8.1	30.4 30.5	30.5	86.4 85.5	86.0	6.2 6.1	6.1		6.3 6.3	6.3		6.4 7.7	7.1	
12-May-14	Sunny	Moderate	11:21	10.4	Surface	1.0	24.0 24.0	24.0	8.0 8.0	8.0	15.4 15.2	15.3	84.8 84.1	84.5	6.5 6.5	6.5	6.4	11.2 11.5	11.4	11.4	3.5 4.3	3.9	4.3
					Middle	5.2	23.7 23.7	23.7	7.9 8.0	8.0	20.0 20.2	20.1	83.2 82.8	83.0	6.3 6.2	6.3		11.5 11.5	11.5		4.6 5.1	4.9	
					Bottom	9.4	23.7 23.7	23.7	7.8 7.9	7.9	24.3 23.6	23.9	84.7 83.8	84.3	6.2 6.2	6.2		11.2 11.4	11.3		3.7 4.6	4.2	
14-May-14	Sunny	Moderate	12:32	10.2	Surface	1.0	25.1 25.2	25.1	8.1 8.1	8.1	17.8 17.7	17.8	83.8 84.3	84.1	6.3 6.3	6.3	6.1	7.8 8.0	7.9	10.1	6.1 5.8	6.0	7.2
					Middle	5.1	24.4 24.4	24.4	8.1 8.1	8.1	23.1 23.1	23.1	80.7 81.2	81.0	5.9 5.9	5.9		10.2 10.5	10.4		8.0 7.9	8.0	
					Bottom	9.2	24.4 24.4	24.4	8.1 8.1	8.1	23.4 23.3	23.4	82.3 81.2	81.8	6.0 5.9	6.0		12.1 11.8	12.0		7.3 7.8	7.6	
16-May-14	Cloudy	Moderate	13:54	11.3	Surface	1.0	25.5 25.4	25.5	8.1 8.1	8.1	17.4 17.6	17.5	81.7 81.5	81.6	6.1 6.1	6.1	6.1	9.9 10.1	10.0	11.2	4.4 4.4	4.4	5.3
					Middle	5.7	25.2 25.2	25.2	8.1 8.1	8.1	20.1 20.2	20.2	81.1 80.9	81.0	6.0 5.9	6.0		11.3 11.1	11.2		4.0 5.1	4.6	
					Bottom	10.3	25.1 25.3	25.2	8.0 8.0	8.0	22.1 22.2	22.2	81.2 81.1	81.2	5.9 5.9	5.9		12.4 12.6	12.5		6.5 7.3	6.9	
19-May-14	Sunny	Rough	16:55	11.1	Surface	1.0	27.0 26.6	26.8	8.1 8.1	8.1	14.5 15.3	14.9	86.8 83.8	85.3	6.4 6.2	6.3	6.2	4.3 4.1	4.2	4.5	4.4 3.6	4.0	4.8
					Middle	5.6	25.9 25.9	25.9	8.1 8.1	8.1	18.2 18.7	18.4	83.6 80.6	82.1	6.1 5.9	6.0		4.5 4.4	4.5		4.5 4.7	4.6	
					Bottom	10.1	25.7 26.0	25.8	8.1 8.0	8.1	20.0 20.1	20.1	78.9 80.7	79.8	5.8 5.9	5.9		4.6 4.8	4.7		6.3 5.5	5.9	
21-May-14	Cloudy	Moderate	18:24	10.1	Surface	1.0	26.6 26.6	26.6	8.0 8.1	8.1	13.5 13.5	13.5	78.9 76.8	77.9	5.9 5.7	5.8	5.6	3.8 3.7	3.8	4.8	4.7 4.0	4.4	5.5
					Middle	5.1	25.8 25.8	25.8	8.0 8.0	8.0	19.4 19.5	19.4	72.9 71.6	72.3	5.3 5.2	5.3		5.4 5.3	5.4		5.2 4.6	4.9	
					Bottom	9.1	25.8 25.8	25.8	8.0 8.0	8.0	19.8 19.9	19.9	74.0 73.3	73.7	5.4 5.3	5.4		5.4 4.9	5.2		6.8 7.3	7.1	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)11 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	08:58	10.5	Surface	1.0	26.3 26.3	26.3	8.1 8.1	8.1	12.8 13.1	12.9	76.5 76.5	76.5	5.7 5.7	5.7	5.6	4.3 4.2	4.3	4.5	3.2 3.5	3.4	4.0
					Middle	5.3	26.0 26.0	26.0	8.1 8.0	8.1	18.8 19.4	19.1	74.3 74.8	74.6	5.4 5.4	5.4		4.5 4.5	4.5		4.3 4.4	4.4	
					Bottom	9.5	25.5 25.9	25.7	8.0 8.0	8.0	22.9 21.6	22.2	73.2 75.6	74.4	5.3 5.4	5.4		4.6 4.6	4.6		3.6 4.6	4.1	
26-May-14	Sunny	Moderate	11:39	10.3	Surface	1.0	27.7 27.7	27.7	8.0 7.9	8.0	9.5 9.4	9.4	72.5 74.6	73.6	5.4 5.6	5.5	5.3	6.3 6.0	6.2	6.6	4.0 4.0	4.0	4.8
					Middle	5.2	26.6 26.4	26.5	7.9 7.9	7.9	15.0 17.8	16.4	67.8 67.0	67.4	5.1 5.0	5.1		6.6 7.0	6.8		5.1 5.3	5.2	
					Bottom	9.3	26.2 26.1	26.1	7.8 7.9	7.9	18.2 18.3	18.2	69.3 67.2	68.3	5.1 4.9	5.0		6.8 6.7	6.8		5.2 4.9	5.1	
28-May-14	Sunny	Moderate	12:20	11.1	Surface	1.0	27.7 27.5	27.6	8.1 8.1	8.1	14.7 14.8	14.7	84.2 84.8	84.5	6.1 6.2	6.1	6.0	1.7 1.6	1.7	1.9	3.1 2.7	2.9	2.9
					Middle	5.6	27.2 26.8	27.0	8.1 8.1	8.1	15.7 15.9	15.8	83.2 80.7	82.0	6.0 5.8	5.9		1.8 2.0	1.9		3.1 2.8	3.0	
					Bottom	10.1	26.7 26.7	26.7	8.1 8.1	8.1	19.9 19.8	19.8	79.5 81.9	80.7	5.8 6.0	5.9		2.0 2.0	2.0		3.0 2.5	2.8	
30-May-14	Sunny	Moderate	14:06	10.4	Surface	1.0	28.1 27.9	28.0	8.2 8.2	8.2	14.5 15.0	14.8	93.9 90.8	92.4	6.8 6.6	6.7	6.3	2.6 2.5	2.6	2.5	2.9 2.3	2.6	2.8
					Middle	5.2	27.1 27.1	27.1	8.1 8.1	8.1	18.7 18.5	18.6	79.5 85.6	82.6	5.7 6.1	5.9		2.5 2.5	2.5		2.9 2.2	2.6	
					Bottom	9.4	26.6 26.6	26.6	8.1 8.1	8.1	23.1 22.4	22.8	80.2 80.3	80.3	5.7 5.7	5.7		2.5 2.5	2.5		2.7 3.6	3.2	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)11 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	07:51	10.4	Surface	1.0	23.9 23.9	23.9	8.2 8.2	8.2	27.2 26.9	27.0	85.5 85.4	85.5	6.2 6.2	6.2	6.2	4.2 4.4	4.3	4.6	5.1 4.9	5.0	4.9
					Middle	5.2	23.8 23.8	23.8	8.2 8.2	8.2	28.0 28.0	28.0	84.9 85.0	85.0	6.1 6.1	6.1		4.5 4.6	4.6		5.3 5.1	5.2	
					Bottom	9.4	23.8 23.9	23.8	8.1 8.2	8.2	28.0 28.0	28.0	84.9 85.1	85.0	6.1 6.1	6.1		4.8 4.8	4.8		4.1 4.8	4.5	
5-May-14	Sunny	Moderate	09:28	10.6	Surface	1.0	24.2 24.2	24.2	8.2 8.2	8.2	25.8 25.7	25.8	89.7 89.3	89.5	6.5 6.5	6.5	6.5	2.7 2.6	2.7	3.1	3.8 4.1	4.0	3.7
					Middle	5.3	24.1 24.1	24.1	8.2 8.2	8.2	27.7 27.7	27.7	89.0 88.9	89.0	6.4 6.4	6.4		3.3 3.4	3.4		3.6 3.7	3.7	
					Bottom	9.6	24.1 24.1	24.1	8.2 8.2	8.2	28.8 28.6	28.7	89.7 89.3	89.5	6.4 6.4	6.4		3.2 3.3	3.3		4.2 2.3	3.3	
7-May-14	Cloudy	Moderate	11:17	10.6	Surface	1.0	23.7 23.7	23.7	8.2 8.2	8.2	30.2 30.2	30.2	86.8 87.2	87.0	6.2 6.2	6.2	6.2	4.5 4.4	4.5	4.8	6.5 6.3	6.4	6.3
					Middle	5.3	23.7 23.7	23.7	8.2 8.2	8.2	30.4 30.4	30.4	86.5 87.0	86.8	6.1 6.2	6.2		4.9 4.7	4.8		6.7 6.5	6.6	
					Bottom	9.6	23.7 23.7	23.7	8.2 8.2	8.2	30.5 30.6	30.6	87.7 86.8	87.3	6.2 6.2	6.2		5.2 4.9	5.1		5.5 6.2	5.9	
9-May-14	Rainy	Moderate	14:57	10.1	Surface	1.0	23.5 23.5	23.5	8.1 8.1	8.1	29.5 29.2	29.3	86.9 89.4	88.2	6.2 6.4	6.3	6.3	6.3 5.8	6.1	6.9	7.6 6.6	7.1	7.6
					Middle	5.1	23.7 23.7	23.7	8.1 8.1	8.1	30.3 30.3	30.3	90.8 86.3	88.6	6.5 6.1	6.3		7.3 7.3	7.3		7.8 6.4	7.1	
					Bottom	9.1	23.6 23.7	23.7	8.1 8.1	8.1	30.2 30.3	30.3	93.2 86.5	89.9	6.6 6.2	6.4		7.3 7.1	7.2		9.3 8.0	8.7	
12-May-14	Sunny	Moderate	17:56	10.5	Surface	1.0	24.7 24.7	24.7	8.0 8.0	8.0	16.8 17.0	16.9	85.0 85.1	85.1	6.4 6.4	6.4	6.4	10.0 9.4	9.7	11.4	4.8 5.1	5.0	4.8
					Middle	5.3	24.2 24.2	24.2	8.0 7.9	8.0	19.2 19.5	19.4	83.7 83.5	83.6	6.3 6.3	6.3		11.3 11.2	11.3		4.6 4.7	4.7	
					Bottom	9.5	23.9 24.0	24.0	7.7 7.9	7.8	24.4 23.3	23.9	84.3 83.5	83.9	6.2 6.2	6.2		13.4 13.2	13.3		5.2 4.3	4.8	
14-May-14	Sunny	Moderate	19:33	10.2	Surface	1.0	25.7 25.7	25.7	8.0 8.0	8.0	15.0 14.8	14.9	85.8 85.2	85.5	6.4 6.4	6.4	6.3	6.5 6.1	6.3	8.0	4.8 4.6	4.7	5.2
					Middle	5.1	25.2 25.2	25.2	8.0 8.0	8.0	21.1 20.9	21.0	84.9 85.9	85.4	6.2 6.3	6.2		8.3 8.6	8.5		3.8 5.7	4.8	
					Bottom	9.2	24.9 25.2	25.1	8.0 8.0	8.0	22.2 21.5	21.9	84.1 85.3	84.7	6.1 6.2	6.2		8.7 9.5	9.1		5.9 6.0	6.0	
16-May-14	Cloudy	Moderate	07:57	11.4	Surface	1.0	25.2 25.3	25.3	8.0 8.0	8.0	19.7 19.6	19.7	80.2 80.0	80.1	5.9 5.9	5.9	5.9	5.0 4.8	4.9	5.3	7.0 8.1	7.6	7.4
					Middle	5.7	25.2 25.2	25.2	8.0 8.0	8.0	19.8 19.9	19.8	79.9 80.1	80.0	5.9 5.9	5.9		5.4 5.4	5.3		7.3 7.7	7.5	
					Bottom	10.4	25.2 25.2	25.2	8.0 8.0	8.0	20.4 20.0	20.2	80.1 79.9	80.0	5.9 5.9	5.9		5.7 5.5	5.6		7.4 6.6	7.0	
19-May-14	Cloudy	Moderate	09:30	11.2	Surface	1.0	25.8 25.8	25.8	8.0 8.0	8.0	16.2 16.2	16.2	72.9 73.4	73.2	5.4 5.5	5.4	5.4	3.5 3.6	3.6	3.8	4.2 5.5	4.9	5.3
					Middle	5.6	25.7 25.7	25.7	8.0 8.0	8.0	16.6 16.6	16.6	73.2 72.9	73.1	5.4 5.4	5.4		3.8 3.8	3.8		4.5 4.9	4.7	
					Bottom	10.2	25.7 25.6	25.7	8.0 8.0	8.0	17.8 18.3	18.1	72.7 73.1	72.9	5.4 5.4	5.4		3.8 3.9	3.9		6.5 5.8	6.2	
21-May-14	Cloudy	Moderate	11:33	10.1	Surface	1.0	26.1 26.0	26.1	8.0 8.1	8.1	13.6 13.3	13.5	74.7 74.0	74.4	5.6 5.6	5.6	5.5	6.8 7.6	7.2	10.4	3.7 3.3	3.5	4.8
					Middle	5.1	25.6 25.6	25.6	8.0 8.0	8.1	20.6 21.2	20.9	72.9 72.7	72.8	5.3 5.3	5.3		12.5 12.3	12.4		5.8 5.5	5.7	
					Bottom	9.1	25.6 25.6	25.6	8.0 8.0	8.0	21.5 21.5	21.5	73.2 72.8	73.0	5.3 5.3	5.3		11.2 11.9	11.6		5.3 5.0	5.2	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)11 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	14:44	10.6	Surface	1.0	26.3 26.4	26.4	7.9 8.0	8.0	15.0 14.9	14.9	82.2 81.8	82.0	6.1 6.1	6.1	6.0	3.3 3.1	3.2	4.0	2.7 4.3	3.5	3.9
					Middle	5.3	26.1 26.1	26.1	7.9 8.0	7.9	16.9 17.0	17.0	79.8 79.0	79.4	5.9 5.8	5.8		4.4 4.3	4.4		3.9 4.0	4.0	
					Bottom	9.6	26.0 25.9	26.0	7.9 7.6	7.8	22.6 22.5	22.5	82.4 85.3	83.9	5.9 6.1	6.0		4.5 4.5	4.5		3.8 4.7	4.3	
26-May-14	Sunny	Moderate	18:00	10.6	Surface	1.0	27.9 27.8	27.8	8.1 8.1	8.1	13.3 13.7	13.5	87.4 85.7	86.6	6.4 6.2	6.3	5.9	5.2 5.3	5.3	5.5	2.9 3.4	3.2	4.0
					Middle	5.3	26.2 27.1	26.7	8.1 8.1	8.1	16.7 15.9	16.3	73.4 73.6	73.5	5.4 5.4	5.4		5.5 5.4	5.5		3.8 3.2	3.5	
					Bottom	9.6	25.8 25.8	25.8	8.0 8.0	8.0	23.3 23.2	23.2	78.5 75.8	77.2	5.6 5.4	5.5		5.8 5.7	5.8		6.6 4.1	5.4	
28-May-14	Sunny	Moderate	19:08	11.1	Surface	1.0	28.0 28.0	28.0	8.1 8.1	8.1	10.1 10.0	10.0	91.9 94.4	93.2	6.8 7.0	6.9	6.8	2.7 2.7	2.7	2.9	4.6 4.1	4.4	5.0
					Middle	5.6	27.5 27.6	27.6	8.1 8.1	8.1	12.6 13.6	13.1	88.0 92.5	90.3	6.5 6.7	6.6		2.9 3.0	3.0		5.5 5.3	5.4	
					Bottom	10.1	27.6 27.5	27.5	8.1 8.1	8.1	15.3 15.5	15.4	91.3 87.7	89.5	6.7 6.4	6.5		3.1 2.9	3.0		5.9 4.7	5.3	
30-May-14	Sunny	Moderate	06:48	10.6	Surface	1.0	27.0 26.9	27.0	8.1 8.1	8.1	16.7 18.1	17.4	73.1 73.4	73.3	5.3 5.3	5.3	5.2	7.4 7.5	7.5	7.4	5.2 5.3	5.3	4.5
					Middle	5.3	26.3 26.2	26.3	8.1 8.1	8.1	24.6 24.7	24.7	72.4 71.4	71.9	5.1 5.0	5.0		7.4 7.2	7.3		3.9 4.4	4.2	
					Bottom	9.6	26.4 26.2	26.3	8.0 8.0	8.0	25.7 25.8	25.8	70.7 73.2	72.0	5.0 5.1	5.0		7.6 7.3	7.5		3.5 4.5	4.0	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)16 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	14:39	6.8	Surface	1.0	24.6 24.6	24.6	8.3 8.3	8.3	26.5 26.5	26.5	90.8 90.9	90.9	6.5 6.5	6.5	6.4	3.3 3.2	3.3	4.4	3.3 3.6	3.5	3.9
					Middle	3.4	24.2 24.2	24.2	8.3 8.3	8.3	27.2 27.2	27.2	88.0 88.4	88.2	6.3 6.4	6.3		4.5 4.4	4.5		3.9 4.5	4.2	
					Bottom	5.8	23.9 23.8	23.8	8.3 8.3	8.3	29.0 28.6	28.8	87.7 87.9	87.8	6.3 6.3	6.3		5.5 5.3	5.4		4.5 3.5	4.0	
5-May-14	Sunny	Moderate	16:38	6.6	Surface	1.0	24.3 24.2	24.2	8.4 8.4	8.4	26.1 25.9	26.0	94.1 92.0	93.1	6.8 6.7	6.7	6.7	3.0 2.7	2.9	2.7	3.6 3.0	3.3	3.2
					Middle	3.3	24.1 24.1	24.1	8.4 8.4	8.4	27.5 28.7	28.1	94.0 91.6	92.8	6.8 6.5	6.6		2.6 2.7	2.7		2.8 2.7	2.8	
					Bottom	5.6	24.0 24.0	24.0	8.4 8.4	8.4	30.3 30.0	30.2	92.8 96.3	94.6	6.6 6.8	6.7		2.5 2.3	2.4		3.6 3.6	3.6	
7-May-14	Cloudy	Moderate	18:04	7.1	Surface	1.0	23.5 23.5	23.5	8.4 8.4	8.4	29.3 29.4	29.3	89.0 93.8	91.4	6.4 6.6	6.5	6.4	6.9 7.0	7.0	7.1	4.7 5.0	4.9	5.3
					Middle	3.6	23.7 23.7	23.7	8.4 8.4	8.4	30.2 30.9	30.6	89.1 87.3	88.2	6.4 6.2	6.3		7.2 7.0	7.1		5.3 5.9	5.6	
					Bottom	6.1	23.7 23.7	23.7	8.4 8.4	8.4	31.3 31.3	31.3	86.0 88.6	87.3	6.1 6.3	6.2		7.2 7.2	7.2		5.9 4.9	5.4	
9-May-14	Rainy	Moderate	14:34	6.5	Surface	1.0	23.3 23.3	23.3	8.3 8.4	8.3	28.0 28.0	28.0	90.5 90.1	90.3	6.6 6.5	6.6	6.6	5.2 5.0	5.1	5.5	12.9 12.4	12.7	13.8
					Middle	3.3	23.4 23.5	23.4	8.4 8.3	8.3	28.0 28.2	28.1	89.0 89.3	89.2	6.5 6.5	6.5		5.5 5.6	5.6		14.3 13.8	14.1	
					Bottom	5.5	23.5 23.4	23.5	8.3 8.3	8.3	29.7 29.5	29.6	93.4 90.7	92.1	6.7 6.5	6.6		5.8 5.8	5.8		15.7 13.4	14.6	
12-May-14	Sunny	Moderate	11:47	7.0	Surface	1.0	23.9 24.2	24.1	8.2 8.2	8.2	18.6 17.1	17.8	92.2 92.9	92.6	6.8 7.1	6.9	6.8	5.1 5.0	5.1	5.3	4.6 4.0	4.3	4.2
					Middle	3.5	23.8 23.8	23.8	8.2 8.3	8.2	19.7 19.6	19.6	89.6 89.9	89.8	6.7 6.5	6.6		5.4 5.2	5.3		3.8 3.7	3.8	
					Bottom	6.0	23.7 24.0	23.9	8.2 8.2	8.2	27.1 25.9	26.5	86.5 88.7	87.6	6.5 6.7	6.6		5.5 5.7	5.6		4.6 4.6	4.6	
14-May-14	Sunny	Moderate	13:06	6.5	Surface	1.0	24.7 24.9	24.8	7.7 7.7	7.7	21.8 21.3	21.6	83.8 85.0	84.4	6.2 6.2	6.2	6.2	5.5 5.2	5.4	5.5	5.3 4.2	4.8	4.9
					Middle	3.3	24.3 24.4	24.4	7.7 7.7	7.7	22.5 22.3	22.4	84.0 83.2	83.6	6.2 6.1	6.2		5.6 5.5	5.6		4.6 5.4	5.0	
					Bottom	5.5	24.2 24.5	24.3	7.7 7.7	7.7	24.5 24.3	24.4	85.7 83.9	84.8	6.3 6.1	6.2		5.5 5.4	5.5		5.3 4.6	5.0	
16-May-14	Cloudy	Moderate	14:04	6.5	Surface	1.0	26.0 26.0	26.0	7.7 7.7	7.7	19.5 19.5	19.5	91.7 88.5	90.1	6.7 6.4	6.6	6.4	4.8 4.9	4.9	5.4	5.0 5.1	5.1	4.7
					Middle	3.3	25.1 25.2	25.2	7.7 7.7	7.7	21.7 21.8	21.8	82.5 84.0	83.3	6.0 6.1	6.1		5.6 5.7	5.7		3.8 4.1	4.0	
					Bottom	5.5	24.7 25.0	24.9	7.6 7.7	7.6	25.4 25.1	25.2	83.9 87.2	85.6	6.0 6.3	6.1		5.6 5.8	5.7		5.4 4.7	5.1	
19-May-14	Sunny	Rough	15:55	6.3	Surface	1.0	26.9 26.6	26.8	7.5 7.5	7.5	17.9 18.0	17.9	87.3 83.8	85.6	6.3 6.1	6.2	6.1	4.1 4.1	4.1	4.2	6.2 7.8	7.0	8.5
					Middle	3.2	26.0 25.9	26.0	7.5 7.5	7.5	19.3 19.7	19.5	81.3 82.1	81.7	5.9 6.0	5.9		4.1 4.2	4.2		8.5 9.0	8.8	
					Bottom	5.3	26.2 25.5	25.9	7.5 7.5	7.5	21.2 22.3	21.8	85.3 82.7	84.0	6.1 6.0	6.0		4.2 4.2	4.2		10.1 9.0	9.6	
21-May-14	Cloudy	Moderate	17:53	6.4	Surface	1.0	26.6 26.4	26.5	7.6 7.6	7.6	16.9 16.9	16.9	82.7 80.4	81.6	6.0 5.9	6.0	5.9	4.6 4.5	4.6	4.6	6.0 6.2	6.1	5.7
					Middle	3.2	25.9 26.0	26.0	7.6 7.6	7.6	18.8 18.9	18.8	78.3 79.8	79.1	5.7 5.8	5.8		4.6 4.5	4.6		6.0 5.1	5.6	
					Bottom	5.4	25.8 25.6	25.7	7.6 7.6	7.6	22.7 23.1	22.9	79.5 82.7	81.1	5.7 5.9	5.8		4.6 4.5	4.6		4.8 6.0	5.4	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)16 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	09:07	6.3	Surface	1.0	26.2 26.2	26.2	7.7 7.7	7.7	16.7 15.9	16.3	81.1 79.0	80.1	6.0 5.8	5.9	5.8	3.6 3.9	3.8	4.2	3.2 2.5	2.9	3.1
					Middle	3.2	25.8 25.7	25.8	7.7 7.7	7.7	20.9 18.8	19.9	76.6 80.3	78.5	5.5 5.9	5.7		4.4 4.2	4.3		3.6 2.8	3.2	
					Bottom	5.3	25.5 25.5	25.5	7.7 7.7	7.7	24.0 24.2	24.1	77.6 82.9	80.3	5.6 5.9	5.7		4.5 4.3	4.4		2.8 3.4	3.1	
26-May-14	Sunny	Moderate	11:48	6.3	Surface	1.0	28.1 28.1	28.1	7.7 7.7	7.7	14.4 14.3	14.3	100.6 99.8	100.2	7.3 7.2	7.2	6.7	2.7 2.5	2.6	3.4	3.3 3.3	3.3	4.3
					Middle	3.2	28.0 27.8	27.9	7.6 7.6	7.6	14.4 15.0	14.7	82.3 85.7	84.0	6.0 6.2	6.1		3.6 3.4	3.5		4.9 4.6	4.8	
					Bottom	5.3	26.5 26.5	26.5	7.5 7.5	7.5	20.1 19.1	19.6	80.6 76.8	78.7	5.8 5.6	5.7		4.0 4.0	4.0		4.8 4.8	4.8	
28-May-14	Sunny	Moderate	12:54	6.1	Surface	1.0	28.6 28.1	28.3	8.6 8.5	8.6	17.3 17.5	17.4	124.3 121.1	122.7	8.8 8.6	8.7	7.2	3.2 3.4	3.3	3.5	5.7 5.2	5.5	6.1
					Middle	3.1	26.8 27.0	26.9	8.2 8.3	8.2	19.8 18.5	19.2	78.4 81.2	79.8	5.6 5.8	5.7		3.6 3.5	3.6		5.8 5.2	5.5	
					Bottom	5.1	26.1 26.2	26.2	8.1 8.2	8.2	23.8 23.5	23.7	79.3 78.0	78.7	5.6 5.5	5.6		3.5 3.6	3.6		6.8 7.8	7.3	
30-May-14	Sunny	Moderate	13:20	7.1	Surface	1.0	28.2 27.8	28.0	8.5 8.4	8.5	19.0 19.0	19.0	96.6 103.0	99.8	6.8 7.1	7.0	6.8	3.2 3.1	3.2	3.3	7.5 6.6	7.1	7.3
					Middle	3.6	26.5 26.7	26.6	8.3 8.3	8.3	21.5 21.8	21.6	86.2 100.3	93.3	6.0 7.1	6.5		3.4 3.3	3.4		7.2 7.0	7.1	
					Bottom	6.1	26.2 26.6	26.4	8.2 8.4	8.3	26.7 26.7	26.7	81.5 94.8	88.2	5.8 6.7	6.3		3.4 3.3	3.4		8.3 7.3	7.8	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)16 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	07:43	6.8	Surface	1.0	23.9 23.9	23.9	8.4 8.5	8.5	26.3 26.1	26.2	87.0 87.0	87.0	6.3 6.3	6.3	6.3	5.0 4.8	4.9	6.3	3.4 2.2	2.8	3.1
					Middle	3.4	23.9 23.9	23.9	8.5 8.4	8.5	26.9 27.0	26.9	86.3 86.4	86.4	6.2 6.3	6.2		6.1 6.2	6.2		3.9 3.1	3.5	
					Bottom	5.8	23.9 23.9	23.9	8.5 8.4	8.5	27.2 27.3	27.3	86.4 86.8	86.6	6.2 6.3	6.3		7.6 7.9	7.8		2.9 2.8	2.9	
5-May-14	Sunny	Moderate	09:21	6.3	Surface	1.0	24.4 24.3	24.3	8.4 8.4	8.4	24.4 24.6	24.5	93.1 92.1	92.6	6.8 6.7	6.7	6.8	2.9 3.0	3.0	3.8	3.9 4.5	4.2	4.5
					Middle	3.2	24.2 24.2	24.2	8.4 8.4	8.4	25.0 25.1	25.1	92.1 93.5	92.8	6.7 6.8	6.8		3.3 3.4	3.4		3.6 4.0	3.8	
					Bottom	5.3	24.1 24.2	24.2	8.4 8.4	8.4	25.7 25.6	25.7	95.5 92.1	93.8	6.9 6.7	6.8		4.9 5.0	5.0		6.1 4.6	5.4	
7-May-14	Cloudy	Moderate	11:17	7.1	Surface	1.0	23.4 23.5	23.4	8.4 8.4	8.4	28.9 29.0	29.0	96.8 86.9	91.9	6.9 6.3	6.6	6.5	3.3 3.3	3.3	3.6	4.8 3.6	4.2	4.5
					Middle	3.6	23.7 23.6	23.6	8.4 8.4	8.4	29.5 29.1	29.3	86.4 92.2	89.3	6.1 6.6	6.4		3.5 3.7	3.6		5.3 4.5	4.9	
					Bottom	6.1	23.7 23.7	23.7	8.4 8.4	8.4	30.8 30.8	30.8	91.5 84.4	88.0	6.6 6.0	6.3		3.7 3.8	3.8		4.3 4.2	4.3	
9-May-14	Rainy	Moderate	09:53	6.4	Surface	1.0	23.5 23.5	23.5	8.4 8.4	8.4	28.7 28.7	28.7	85.9 90.6	88.3	6.2 6.5	6.4	6.4	9.5 9.5	9.5	9.5	6.4 5.9	6.2	8.4
					Middle	3.2	23.6 23.6	23.6	8.3 8.3	8.3	29.0 30.1	29.5	91.1 84.8	88.0	6.6 6.1	6.3		9.5 9.5	9.5		8.2 8.2	8.2	
					Bottom	5.4	23.6 23.6	23.6	8.3 8.4	8.3	30.1 30.3	30.2	95.0 89.7	92.4	6.8 6.4	6.6		9.5 9.5	9.5		11.0 10.6	10.8	
12-May-14	Sunny	Moderate	17:15	7.1	Surface	1.0	24.8 24.5	24.6	8.2 8.2	8.2	17.2 17.3	17.3	95.3 89.3	92.3	6.9 6.6	6.8	6.8	6.3 6.2	6.3	6.6	4.9 5.5	5.2	5.5
					Middle	3.6	24.0 23.8	23.9	8.2 8.2	8.2	18.6 18.6	18.6	87.7 91.0	89.4	6.5 6.8	6.7		6.5 6.6	6.6		4.6 5.0	4.8	
					Bottom	6.1	24.3 24.1	24.2	8.1 8.1	8.1	27.0 25.8	26.4	86.2 90.1	88.2	6.4 6.8	6.6		6.6 6.9	6.8		7.1 5.6	6.4	
14-May-14	Sunny	Moderate	19:09	6.5	Surface	1.0	25.3 25.3	25.3	7.7 7.7	7.7	21.2 21.2	21.2	88.7 87.7	88.2	6.5 6.4	6.4	6.4	8.5 8.6	8.6	8.7	7.1 6.9	7.0	5.9
					Middle	3.3	25.2 25.1	25.2	7.7 7.6	7.7	21.4 21.4	21.4	87.6 85.0	86.3	6.4 6.2	6.3		8.8 8.6	8.7		4.2 5.2	4.7	
					Bottom	5.5	25.3 24.7	25.0	7.7 7.6	7.6	22.3 22.8	22.5	88.1 84.3	86.2	6.4 6.2	6.3		8.9 8.9	8.9		5.6 6.2	5.9	
16-May-14	Cloudy	Moderate	07:05	6.5	Surface	1.0	25.6 25.5	25.6	7.6 7.6	7.6	17.0 16.9	16.9	82.0 81.2	81.6	6.1 6.0	6.1	6.1	6.0 6.2	6.1	7.6	6.7 6.5	6.6	6.5
					Middle	3.3	25.4 25.4	25.4	7.7 7.7	7.7	17.5 18.9	18.2	82.1 80.6	81.4	6.1 5.9	6.0		8.3 8.1	8.2		6.9 6.6	6.8	
					Bottom	5.5	25.2 25.1	25.1	7.6 7.6	7.6	21.7 21.6	21.7	80.6 83.4	82.0	5.9 6.1	6.0		8.2 8.5	8.4		6.5 5.7	6.1	
19-May-14	Cloudy	Moderate	09:33	6.4	Surface	1.0	26.1 26.0	26.1	7.5 7.5	7.5	15.1 15.2	15.1	77.4 77.9	77.7	5.8 5.8	5.8	5.8	3.8 3.9	3.9	4.2	5.1 6.2	5.7	6.2
					Middle	3.2	26.0 26.0	26.0	7.5 7.5	7.5	16.2 15.8	16.0	77.4 78.7	78.1	5.7 5.8	5.8		4.3 4.3	4.3		6.1 6.2	6.2	
					Bottom	5.4	26.0 26.0	26.0	7.5 7.5	7.5	17.0 18.1	17.6	80.7 77.6	79.2	5.9 5.7	5.8		4.4 4.1	4.3		7.3 6.2	6.8	
21-May-14	Cloudy	Moderate	11:23	6.3	Surface	1.0	26.2 26.2	26.2	7.6 7.6	7.6	14.9 14.9	14.9	81.0 80.8	80.9	6.0 6.0	6.0	6.0	9.6 9.6	9.6	10.1	7.4 6.9	7.2	6.9
					Middle	3.2	26.2 26.2	26.2	7.6 7.6	7.6	15.1 15.2	15.1	80.1 80.0	80.1	5.9 5.9	5.9		10.1 10.4	10.3		7.1 6.8	7.0	
					Bottom	5.3	26.2 26.2	26.2	7.5 7.6	7.6	17.1 17.2	17.1	80.9 80.7	80.8	6.0 5.9	5.9		10.5 10.4	10.5		6.2 6.8	6.5	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS(Mf)16 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	14:07	6.1	Surface	1.0	26.4 <u>26.4</u>	26.4	7.6 <u>7.6</u>	7.6	14.4 <u>14.2</u>	14.3	84.9 <u>84.2</u>	84.6	6.3 <u>6.3</u>	6.3	6.2	4.5 <u>4.9</u>	4.7	6.4	3.2 <u>4.4</u>	3.8	3.8
					Middle	3.1	26.3 <u>26.3</u>	26.3	7.6 <u>7.6</u>	7.6	16.0 <u>15.3</u>	15.6	81.6 <u>81.4</u>	81.5	6.0 <u>6.0</u>	6.0		6.1 <u>6.6</u>	6.4		3.9 <u>2.3</u>	3.1	
					Bottom	5.1	26.1 <u>26.2</u>	26.1	7.6 <u>7.6</u>	7.6	19.0 <u>19.1</u>	19.1	82.3 <u>82.9</u>	82.6	6.0 <u>6.0</u>	6.0		8.3 <u>7.6</u>	8.0		3.9 <u>4.9</u>	4.4	
26-May-14	Sunny	Moderate	18:09	6.4	Surface	1.0	28.1 <u>28.3</u>	28.2	7.7 <u>7.7</u>	7.7	12.6 <u>12.5</u>	12.5	97.4 <u>102.2</u>	99.8	7.1 <u>7.4</u>	7.3	7.0	7.1 <u>7.3</u>	7.2	8.3	3.6 <u>3.6</u>	3.6	3.9
					Middle	3.2	27.4 <u>27.4</u>	27.4	7.6 <u>7.5</u>	7.6	13.7 <u>13.6</u>	13.7	90.0 <u>89.4</u>	89.7	6.6 <u>6.6</u>	6.6		8.0 <u>7.8</u>	7.9		3.9 <u>4.3</u>	4.1	
					Bottom	5.4	26.5 <u>27.3</u>	26.9	7.5 <u>7.5</u>	7.5	21.3 <u>18.5</u>	19.9	84.6 <u>92.0</u>	88.3	6.0 <u>6.6</u>	6.3		10.5 <u>9.3</u>	9.9		3.8 <u>4.3</u>	4.1	
28-May-14	Sunny	Moderate	19:27	6.5	Surface	1.0	28.5 <u>28.9</u>	28.7	8.7 <u>8.6</u>	8.6	17.6 <u>17.3</u>	17.5	138.8 <u>142.9</u>	140.9	9.8 <u>10.0</u>	9.9	9.0	7.5 <u>7.5</u>	7.5	7.6	6.8 <u>6.8</u>	6.8	7.3
					Middle	3.3	28.3 <u>27.6</u>	28.0	8.6 <u>8.5</u>	8.6	17.7 <u>17.9</u>	17.8	115.2 <u>110.2</u>	112.7	8.1 <u>7.9</u>	8.0		7.8 <u>7.6</u>	7.7		6.2 <u>7.2</u>	6.7	
					Bottom	5.5	27.4 <u>26.6</u>	27.0	8.4 <u>8.2</u>	8.3	19.0 <u>22.2</u>	20.6	97.3 <u>92.1</u>	94.7	6.9 <u>6.5</u>	6.7		7.7 <u>7.5</u>	7.6		8.0 <u>8.5</u>	8.3	
30-May-14	Sunny	Moderate	06:47	7.3	Surface	1.0	27.4 <u>27.3</u>	27.4	8.3 <u>8.3</u>	8.3	16.8 <u>17.7</u>	17.3	86.1 <u>88.0</u>	87.1	6.2 <u>6.2</u>	6.2	6.1	2.9 <u>2.8</u>	2.9	3.1	4.2 <u>3.4</u>	3.8	3.6
					Middle	3.7	26.8 <u>26.9</u>	26.9	8.2 <u>8.2</u>	8.2	20.1 <u>19.0</u>	19.5	84.9 <u>81.5</u>	83.2	6.1 <u>5.8</u>	5.9		3.0 <u>3.1</u>	3.1		2.6 <u>3.5</u>	3.1	
					Bottom	6.3	26.9 <u>26.8</u>	26.9	8.2 <u>8.2</u>	8.2	21.9 <u>22.0</u>	22.0	78.1 <u>80.4</u>	79.3	5.6 <u>5.7</u>	5.7		3.2 <u>3.3</u>	3.3		3.8 <u>3.9</u>	3.9	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	13:51	9.4	Surface	1.0	24.2 24.1	24.2	8.3 8.3	8.3	28.4 28.1	28.3	92.7 92.9	92.8	6.6 6.7	6.6	6.6	5.7 5.7	5.7	5.8	3.4 3.3	3.4	4.3
					Middle	4.7	24.1 24.1	24.1	8.3 8.3	8.3	29.0 29.2	29.1	92.6 92.6	92.6	6.6 6.6	6.6		5.8 5.8	5.8		5.0 4.7	4.9	
					Bottom	8.4	24.1 24.1	24.1	8.2 8.3	8.3	29.5 29.6	29.5	91.9 92.2	92.1	6.5 6.5	6.5		6.0 5.8	5.9		4.6 4.7	4.7	
5-May-14	Sunny	Moderate	15:42	8.8	Surface	1.0	24.4 24.4	24.4	8.4 8.4	8.4	28.3 28.3	28.3	93.1 93.0	93.1	6.6 6.6	6.6	6.6	3.7 3.9	3.8	3.8	5.5 4.7	5.1	5.6
					Middle	4.4	24.4 24.4	24.4	8.4 8.4	8.4	28.4 28.5	28.5	92.4 92.4	92.4	6.6 6.6	6.6		3.8 3.7	3.8		5.2 6.8	6.0	
					Bottom	7.8	24.4 24.4	24.4	8.4 8.4	8.4	28.6 28.5	28.5	92.6 92.6	92.6	6.6 6.6	6.6		3.7 3.8	3.8		5.7 5.4	5.6	
7-May-14	Cloudy	Moderate	17:18	9.1	Surface	1.0	23.5 23.4	23.5	8.5 8.5	8.5	28.6 28.5	28.6	89.8 91.1	90.5	6.4 6.5	6.5	6.5	6.2 6.1	6.2	6.4	5.2 4.7	5.0	5.8
					Middle	4.6	23.7 23.7	23.7	8.5 8.5	8.5	31.0 31.2	31.1	89.5 89.9	89.7	6.3 6.4	6.4		6.5 6.4	6.5		6.4 6.1	6.3	
					Bottom	8.1	23.7 23.7	23.7	8.4 8.5	8.5	31.8 31.9	31.9	89.8 89.3	89.6	6.4 6.3	6.4		6.6 6.6	6.6		6.0 6.1	6.1	
9-May-14	Rainy	Moderate	13:55	8.5	Surface	1.0	23.4 23.5	23.5	8.4 8.4	8.4	26.1 26.3	26.2	88.7 89.0	88.9	6.5 6.5	6.5	6.5	7.6 7.6	7.6	8.3	10.0 9.0	9.5	12.3
					Middle	4.3	23.6 23.6	23.6	8.4 8.4	8.4	28.7 28.5	28.6	88.5 88.9	88.7	6.4 6.4	6.4		8.5 8.6	8.6		10.5 12.2	11.4	
					Bottom	7.5	23.6 23.6	23.6	8.3 8.4	8.4	29.5 29.6	29.5	90.1 88.9	89.5	6.5 6.4	6.4		8.4 8.8	8.6		16.4 15.4	15.9	
12-May-14	Sunny	Moderate	12:29	9.3	Surface	1.0	23.9 24.1	24.0	8.3 8.3	8.3	16.1 14.2	15.2	87.1 87.9	87.5	6.7 6.8	6.8	6.5	8.0 8.2	8.1	8.3	6.8 5.7	6.3	6.6
					Middle	4.7	23.6 23.6	23.6	8.3 8.3	8.3	27.1 27.6	27.3	86.1 85.7	85.9	6.2 6.2	6.2		8.3 8.2	8.3		7.8 7.0	7.0	
					Bottom	8.3	23.6 23.6	23.6	8.3 8.3	8.3	28.2 28.0	28.1	85.1 85.0	85.1	6.2 6.2	6.2		8.2 8.6	8.4		6.7 6.4	6.6	
14-May-14	Sunny	Moderate	13:54	8.5	Surface	1.0	25.3 25.7	25.5	7.8 7.7	7.8	20.9 20.3	20.6	89.8 91.6	90.7	6.6 6.7	6.6	6.5	9.5 9.9	9.7	10.9	6.5 7.0	6.8	7.5
					Middle	4.3	24.5 24.6	24.5	7.8 7.8	7.8	26.9 26.2	26.6	87.6 87.8	87.7	6.3 6.3	6.3		11.2 11.3	11.3		7.1 7.4	7.3	
					Bottom	7.5	24.0 24.1	24.0	7.8 7.8	7.8	28.6 28.4	28.5	87.6 88.3	88.0	6.3 6.3	6.3		11.5 11.7	11.6		8.5 8.3	8.4	
16-May-14	Cloudy	Moderate	12:54	8.5	Surface	1.0	25.8 25.8	25.8	7.6 7.6	7.6	21.0 20.6	20.8	87.0 86.8	86.9	6.3 6.3	6.3	6.2	16.6 16.3	16.5	16.5	10.8 9.9	10.4	10.0
					Middle	4.3	25.1 25.0	25.1	7.7 7.7	7.7	24.0 23.9	24.0	84.6 84.1	84.4	6.1 6.1	6.1		16.7 16.2	16.5		10.1 10.0	10.1	
					Bottom	7.5	25.0 25.0	25.0	7.6 7.6	7.6	25.8 25.8	25.8	85.6 84.8	85.2	6.1 6.1	6.1		16.3 16.6	16.5		9.6 9.4	9.5	
19-May-14	Sunny	Rough	15:09	8.4	Surface	1.0	26.7 26.6	26.6	7.5 7.5	7.5	17.7 17.8	17.7	85.0 83.1	84.1	6.2 6.0	6.1	6.0	10.1 10.2	10.2	10.3	10.3 9.1	9.7	11.8
					Middle	4.2	25.9 26.0	26.0	7.5 7.5	7.5	20.9 19.5	20.2	79.4 81.8	80.6	5.7 5.9	5.8		10.5 10.3	10.4		12.8 12.8	12.8	
					Bottom	7.4	25.5 25.9	25.7	7.5 7.5	7.5	23.5 22.9	23.2	79.5 83.0	81.3	5.7 5.9	5.8		10.5 10.3	10.4		12.9 12.9	12.9	
21-May-14	Cloudy	Moderate	17:08	8.7	Surface	1.0	26.8 26.6	26.7	7.6 7.6	7.6	16.5 16.9	16.7	82.1 79.9	81.0	6.0 5.8	5.9	5.7	5.7 5.6	5.7	6.3	4.2 5.8	5.0	5.9
					Middle	4.4	26.0 26.1	26.0	7.6 7.6	7.6	19.6 19.2	19.4	75.9 74.1	75.0	5.5 5.4	5.5		6.3 6.4	6.4		5.2 6.1	5.7	
					Bottom	7.7	25.4 25.8	25.6	7.6 7.6	7.6	26.0 25.6	25.8	75.0 79.2	77.1	5.3 5.6	5.4		6.7 6.8	6.8		6.9 7.0	7.0	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	10:02	8.4	Surface	1.0	26.2 26.3	26.3	7.7 7.7	7.7	15.8 15.6	15.7	72.2 73.5	72.9	5.3 5.4	5.4	5.4	7.7 8.0	7.9	9.7	4.7 4.3	4.5	4.8
					Middle	4.2	25.5 25.7	25.6	7.6 7.6	7.6	24.1 21.4	22.8	72.0 71.9	72.0	5.3 5.3	5.3		11.3 12.2	11.8		5.5 5.1	5.3	
					Bottom	7.4	25.8 25.3	25.5	7.6 7.6	7.6	23.6 25.7	24.6	75.7 70.0	72.9	5.4 5.0	5.2		5.2	9.4 9.6		9.5	4.1 5.0	
26-May-14	Sunny	Moderate	12:39	8.3	Surface	1.0	28.0 27.6	27.8	7.6 7.6	7.6	14.1 15.5	14.8	83.7 85.5	84.6	6.1 6.1	6.1	5.7	7.0 7.3	7.2	10.1	2.8 3.0	2.9	4.0
					Middle	4.2	25.4 25.6	25.5	7.5 7.5	7.5	25.9 24.6	25.3	71.1 75.9	73.5	5.1 5.5	5.3		11.3 10.8	11.1		4.3 4.3	4.3	
					Bottom	7.3	25.6 25.4	25.5	7.5 7.5	7.5	25.9 26.3	26.1	74.0 69.5	71.8	5.2 4.9	5.1		5.1	12.2 12.0		12.1	4.6 5.0	
28-May-14	Sunny	Moderate	13:51	8.1	Surface	1.0	28.3 28.5	28.4	8.5 8.5	8.5	18.2 17.8	18.0	122.1 120.7	121.4	8.6 8.5	8.5	7.3	6.5 6.8	6.7	8.0	5.0 4.6	4.8	4.8
					Middle	4.1	26.0 25.5	25.8	8.2 8.2	8.2	26.4 26.8	26.6	87.8 84.4	86.1	6.2 5.9	6.1		8.0 8.1	8.1		4.0 5.1	4.6	
					Bottom	7.1	25.4 25.4	25.4	8.2 8.2	8.2	28.7 28.6	28.7	74.9 71.9	73.4	5.2 5.1	5.1		5.1	9.3 9.2		9.3	5.5 4.7	
30-May-14	Sunny	Moderate	12:36	9.5	Surface	1.0	28.1 27.9	28.0	8.5 8.5	8.5	19.6 19.8	19.7	110.1 97.9	104.0	7.7 6.9	7.3	6.9	2.1 2.1	2.1	2.2	5.4 4.6	5.0	4.8
					Middle	4.8	27.4 27.0	27.2	8.3 8.3	8.3	21.0 21.7	21.3	91.8 94.9	93.4	6.4 6.6	6.5		2.2 2.2	2.2		3.9 4.9	4.4	
					Bottom	8.5	26.1 26.0	26.1	8.2 8.1	8.2	27.4 27.6	27.5	82.7 77.9	80.3	5.8 5.5	5.7		5.7	2.3 2.3		2.3	5.6 4.6	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	08:30	9.4	Surface	1.0	23.9 23.9	23.9	8.3 8.3	8.3	26.4 26.4	26.4	87.9 87.7	87.8	6.4 6.4	6.4	6.4	4.5 4.2	4.4	4.6	5.2 5.8	5.5	5.1
					Middle	4.7	23.9 23.9	23.9	8.4 8.3	8.4	26.5 26.4	26.4	87.5 87.7	87.6	6.3 6.4	6.4		4.5 4.7	4.6		4.9 5.2	5.1	
					Bottom	8.4	23.9 23.9	23.9	8.4 8.3	8.4	26.6 26.5	26.6	87.5 87.4	87.5	6.3 6.3	6.3		4.8 4.7	4.8		5.3 4.0	4.7	
5-May-14	Sunny	Moderate	10:10	8.9	Surface	1.0	24.1 24.2	24.2	8.4 8.4	8.4	26.5 26.5	26.5	94.8 94.6	94.7	6.9 6.8	6.8	6.8	2.8 2.6	2.7	2.7	3.7 4.1	3.9	3.9
					Middle	4.5	24.2 24.2	24.2	8.4 8.4	8.4	26.6 26.6	26.6	95.0 94.5	94.8	6.9 6.8	6.8		2.6 2.5	2.6		3.0 3.6	3.3	
					Bottom	7.9	24.2 24.2	24.2	8.4 8.4	8.4	26.5 26.6	26.6	94.5 96.5	94.5	6.8 7.0	6.9		2.7 2.8	2.8		5.2 3.8	4.5	
7-May-14	Cloudy	Moderate	12:01	9.2	Surface	1.0	23.3 23.2	23.3	8.4 8.4	8.4	27.6 27.7	27.7	90.3 90.2	90.3	6.5 6.5	6.5	6.5	4.2 4.5	4.4	4.6	7.0 7.2	7.1	6.6
					Middle	4.6	23.6 23.7	23.6	8.4 8.4	8.4	30.0 30.0	30.0	89.0 89.6	89.3	6.4 6.4	6.4		4.5 4.7	4.6		6.3 6.6	6.5	
					Bottom	8.2	23.7 23.6	23.7	8.4 8.4	8.4	31.3 31.4	31.3	89.2 88.9	89.1	6.4 6.4	6.4		4.7 4.8	4.8		6.7 5.4	6.1	
9-May-14	Rainy	Moderate	10:39	8.2	Surface	1.0	23.5 23.4	23.5	8.4 8.4	8.4	26.8 26.3	26.5	89.6 90.0	89.8	6.5 6.6	6.6	6.5	9.1 8.9	9.0	10.7	5.1 5.8	5.5	6.7
					Middle	4.1	23.6 23.6	23.6	8.4 8.4	8.4	28.3 27.7	28.0	89.3 89.1	89.2	6.4 6.5	6.4		11.4 11.5	11.5		6.4 6.5	6.5	
					Bottom	7.2	23.6 23.6	23.6	8.4 8.4	8.4	29.1 29.2	29.2	90.0 90.5	90.3	6.5 6.5	6.5		11.8 11.2	11.5		7.5 8.5	8.0	
12-May-14	Sunny	Moderate	16:31	9.1	Surface	1.0	24.6 24.8	24.7	8.1 8.1	8.1	17.0 17.3	17.2	86.5 89.6	88.1	6.5 6.6	6.6	6.5	4.9 5.0	5.0	5.1	5.0 5.1	5.1	5.0
					Middle	4.6	23.9 23.9	23.9	8.1 8.1	8.1	21.8 21.4	21.6	88.3 86.3	87.3	6.6 6.3	6.4		5.2 5.0	5.1		4.6 4.6	4.3	
					Bottom	8.1	23.9 24.0	23.9	8.0 8.1	8.0	24.7 24.3	24.5	86.2 84.4	85.3	6.4 6.3	6.4		5.2 5.2	5.2		6.2 4.8	5.5	
14-May-14	Sunny	Moderate	18:26	8.8	Surface	1.0	25.4 25.4	25.4	7.6 7.6	7.6	22.4 22.4	22.4	84.1 84.4	84.3	6.1 6.1	6.1	6.1	10.9 10.4	10.7	11.6	5.2 6.0	5.6	5.8
					Middle	4.4	24.7 25.1	24.9	7.6 7.6	7.6	23.6 22.9	23.2	82.0 83.1	82.6	6.0 6.0	6.0		11.6 11.8	11.7		6.5 5.0	5.8	
					Bottom	7.8	24.5 25.0	24.7	7.6 7.6	7.6	25.0 24.6	24.8	83.2 83.5	83.4	6.0 6.0	6.0		12.3 12.4	12.4		6.2 6.0	6.1	
16-May-14	Cloudy	Moderate	07:52	8.9	Surface	1.0	25.7 25.7	25.7	7.6 7.7	7.7	18.5 18.7	18.6	86.2 85.4	85.8	6.3 6.3	6.3	6.3	5.5 5.5	5.5	6.5	5.0 5.9	5.5	6.1
					Middle	4.5	25.7 25.8	25.7	7.7 7.6	7.7	19.0 19.0	19.0	84.7 86.2	85.5	6.2 6.3	6.3		6.7 6.8	6.8		6.4 6.7	6.6	
					Bottom	7.9	25.8 25.7	25.7	7.6 7.6	7.6	19.8 20.7	20.3	88.3 85.4	86.9	6.4 6.2	6.3		7.4 7.2	7.3		6.4 5.9	6.2	
19-May-14	Cloudy	Moderate	10:26	8.7	Surface	1.0	26.4 26.3	26.4	7.6 7.6	7.6	17.5 17.7	17.6	83.8 83.5	83.7	6.1 6.1	6.1	6.0	4.8 4.9	4.9	5.7	4.1 3.8	4.0	4.2
					Middle	4.4	26.2 26.2	26.2	7.6 7.6	7.6	18.2 18.2	18.2	80.9 81.5	81.2	5.9 5.9	5.9		6.1 6.2	6.2		4.3 4.4	4.4	
					Bottom	7.7	26.0 26.2	26.1	7.6 7.6	7.6	20.3 20.1	20.2	82.1 82.8	82.5	5.9 6.0	6.0		6.2 6.0	6.1		4.3 4.3	4.3	
21-May-14	Cloudy	Moderate	12:09	8.9	Surface	1.0	26.5 26.5	26.5	7.6 7.7	7.7	15.7 15.8	15.7	83.2 79.6	81.4	6.1 5.9	6.0	5.8	4.9 4.9	4.9	7.2	4.6 3.0	3.8	4.2
					Middle	4.5	26.3 26.1	26.2	7.6 7.7	7.7	17.9 18.4	18.1	76.9 76.4	76.7	5.6 5.6	5.6		8.0 8.5	8.3		4.9 4.4	4.7	
					Bottom	7.9	25.7 26.0	25.8	7.6 7.6	7.6	17.9 17.9	17.9	76.4 80.0	78.2	5.5 5.7	5.6		8.4 8.1	8.3		4.6 3.8	4.2	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	13:16	8.2	Surface	1.0	26.4 26.3	26.3	7.7 7.7	7.7	17.1 17.9	17.5	77.5 77.4	77.5	5.7 5.7	5.7	5.4	7.2 7.3	7.3	10.9	3.2 4.0	3.6	3.6
					Middle	4.1	25.7 25.7	25.7	7.6 7.7	7.7	21.7 22.0	21.8	69.9 70.7	70.3	5.0 5.1	5.1		13.3 12.2	12.8		3.4 3.1	3.3	
					Bottom	7.2	25.6 25.6	25.6	7.6 7.6	7.6	23.1 23.2	23.1	73.2 71.0	72.1	5.3 5.1	5.2		12.4 13.0	12.7		3.4 4.3	3.9	
26-May-14	Sunny	Moderate	17:08	8.4	Surface	1.0	28.4 28.6	28.5	7.8 7.8	7.8	14.7 14.6	14.7	109.1 113.5	111.3	7.8 8.1	8.0	7.5	4.8 5.0	4.9	7.4	4.3 3.6	4.0	4.8
					Middle	4.2	27.9 27.9	27.9	7.7 7.7	7.7	16.0 16.2	16.1	94.7 101.0	97.9	6.8 7.2	7.0		7.7 7.0	7.4		4.6 5.1	4.9	
					Bottom	7.4	27.6 27.2	27.4	7.7 7.6	7.6	17.1 17.6	17.4	88.7 86.6	87.7	6.4 6.2	6.3		9.6 10.1	9.9		5.1 5.6	5.4	
28-May-14	Sunny	Moderate	18:40	8.5	Surface	1.0	28.3 28.3	28.3	8.7 8.7	8.7	19.2 19.4	19.3	123.3 130.9	127.1	8.6 9.2	8.9	7.4	7.5 7.1	7.3	7.4	6.7 6.7	6.7	7.2
					Middle	4.3	26.4 26.9	26.6	8.3 8.4	8.3	24.7 23.0	23.8	84.2 82.6	83.4	5.9 5.8	5.8		7.4 7.5	7.5		6.7 7.5	7.1	
					Bottom	7.5	26.1 26.0	26.1	8.2 8.2	8.2	25.7 26.4	26.1	78.9 79.5	79.2	5.5 5.6	5.5		7.3 7.3	7.3		8.3 7.5	7.9	
30-May-14	Sunny	Moderate	07:31	9.3	Surface	1.0	27.6 27.7	27.6	8.4 8.4	8.4	17.0 17.0	17.0	98.6 98.7	98.7	7.1 7.1	7.1	7.0	1.9 1.9	1.9	2.0	6.1 6.2	6.2	6.3
					Middle	4.7	27.5 27.3	27.4	8.4 8.3	8.3	19.1 19.2	19.1	97.7 98.4	98.1	6.8 6.9	6.9		2.0 2.0	2.0		6.6 5.7	6.2	
					Bottom	8.3	27.2 27.1	27.2	8.3 8.3	8.3	22.5 22.8	22.7	91.7 89.3	90.5	6.5 6.4	6.4		2.1 2.2	2.2		6.5 6.5	6.5	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS7 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-May-14	Sunny	Moderate	14:04	3.5	Surface	1.0	24.7 24.7	24.7	8.3 8.3	8.3	26.7 26.6	26.7	93.8 93.9	93.9	6.7 6.7	6.7	6.7	2.8 2.8	2.8	2.9	3.3 4.2	3.8	3.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.5	24.7 24.7	24.7	8.3 8.3	8.3	26.7 26.7	26.7	93.9 93.8	93.9	6.7 6.7	6.7		3.0 2.9	3.0		6.7	3.0 2.9		3.0	2.7 4.5	3.6
5-May-14	Sunny	Moderate	16:00	3.1	Surface	1.0	24.5 24.5	24.5	8.4 8.4	8.4	25.7 25.7	25.7	97.4 98.1	97.8	7.0 7.1	7.0	7.0	2.8 2.5	2.7	3.0	3.9 3.9	3.9	3.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.1	24.5 24.5	24.5	8.4 8.4	8.4	26.9 26.9	26.9	97.5 98.8	98.2	7.0 7.1	7.0		3.4 3.0	3.2		7.0	3.4 3.0		3.2	4.4 3.2	3.8
7-May-14	Cloudy	Moderate	17:31	3.4	Surface	1.0	23.3 23.2	23.3	8.4 8.4	8.4	27.7 27.7	27.7	99.3 92.7	96.0	7.2 6.8	7.0	7.0	7.6 7.7	7.7	7.8	4.7 5.6	5.2	5.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.4	23.2 23.2	23.2	8.4 8.4	8.4	27.6 28.2	27.9	91.6 93.8	92.7	6.7 6.8	6.8		7.7 7.8	7.8		6.8	7.7 7.8		7.8	4.1 5.9	5.0
9-May-14	Rainy	Moderate	14:05	3.3	Surface	1.0	23.1 23.1	23.1	8.4 8.3	8.4	26.9 27.0	27.0	94.2 93.8	94.0	6.9 6.9	6.9	6.9	4.3 4.3	4.3	4.4	7.8 7.1	7.5	8.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	23.2 23.1	23.1	8.3 8.4	8.3	27.3 27.0	27.2	93.9 93.9	93.9	6.9 6.9	6.9		4.4 4.4	4.4		6.9	4.4 4.4		4.4	8.3 9.9	9.1
12-May-14	Sunny	Moderate	12:16	3.4	Surface	1.0	23.9 24.2	24.0	8.1 8.1	8.1	17.4 17.6	17.5	88.1 95.3	91.7	6.6 7.2	6.9	6.9	5.5 5.5	5.5	5.6	4.9 4.9	4.9	4.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.4	23.9 23.9	23.9	8.1 8.1	8.1	20.0 19.6	19.8	89.9 86.3	88.1	6.8 6.6	6.7		5.8 5.5	5.7		6.7	5.8 5.5		5.7	5.4 4.2	4.8
14-May-14	Sunny	Moderate	13:39	3.2	Surface	1.0	25.4 25.3	25.3	7.7 7.7	7.7	20.1 20.4	20.2	87.9 87.6	87.8	6.4 6.4	6.4	6.4	8.5 8.4	8.5	8.7	4.1 4.0	4.1	4.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	25.0 25.1	25.1	7.6 7.7	7.6	21.1 20.9	21.0	88.8 87.2	88.0	6.5 6.4	6.4		8.9 8.7	8.8		6.4	8.9 8.7		8.8	4.2 4.0	4.1
16-May-14	Cloudy	Moderate	13:15	3.3	Surface	1.0	26.0 26.0	26.0	7.6 7.6	7.6	18.1 18.3	18.2	89.3 89.6	89.5	6.5 6.6	6.5	6.5	9.8 9.9	9.9	9.8	5.9 5.1	5.5	6.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.3	26.0 26.0	26.0	7.6 7.6	7.6	18.3 18.6	18.5	89.3 90.8	90.1	6.5 6.6	6.6		9.8 9.6	9.7		6.6	9.8 9.6		9.7	6.7 7.7	7.2
19-May-14	Sunny	Rough	15:23	3.2	Surface	1.0	26.8 26.8	26.8	7.5 7.5	7.5	15.7 15.7	15.7	91.7 90.5	91.1	6.7 6.6	6.7	6.7	2.9 2.7	2.8	2.9	3.9 4.0	4.0	4.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	26.7 26.7	26.7	7.5 7.5	7.5	16.0 16.3	16.1	90.7 92.7	91.7	6.6 6.8	6.7		2.9 2.8	2.9		6.7	2.9 2.8		2.9	4.4 4.2	4.3
21-May-14	Cloudy	Moderate	17:24	3.2	Surface	1.0	27.0 27.1	27.1	7.6 7.6	7.6	15.4 15.4	15.4	94.2 94.6	94.4	6.9 6.9	6.9	6.9	3.4 3.6	3.5	3.6	5.3 6.2	5.8	5.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.2	26.9 27.0	27.0	7.5 7.6	7.6	15.5 15.4	15.5	94.1 94.5	94.3	6.9 6.9	6.9		3.5 3.6	3.6		6.9	3.5 3.6		3.6	6.1 4.8	5.5

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS7 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	09:42	3.3	Surface	1.0	26.6 <u>26.6</u>	26.6	7.6 <u>7.4</u>	7.5	15.3 <u>15.2</u>	15.3	90.2 <u>93.4</u>	91.8	6.6 <u>6.9</u>	6.8	6.8	12.2 <u>11.8</u>	12.0	14.7	4.5 <u>4.7</u>	4.6	4.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.3	26.6 <u>26.6</u>	26.6	7.3 <u>7.5</u>	7.4	15.3 <u>15.3</u>	15.3	96.4 <u>91.4</u>	93.9	7.1 <u>6.7</u>	6.9		6.9	17.7 <u>16.9</u>		17.3	4.7 <u>4.0</u>		4.4			
26-May-14	Sunny	Moderate	12:20	3.3	Surface	1.0	27.8 <u>27.6</u>	27.7	7.6 <u>7.6</u>	7.6	14.3 <u>14.5</u>	14.4	88.4 <u>87.6</u>	88.0	6.4 <u>6.4</u>	6.4	6.4	6.0 <u>6.7</u>	6.4	7.1	2.8 <u>3.0</u>	2.9	3.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.3	27.2 <u>27.3</u>	27.3	7.5 <u>7.5</u>	7.5	18.3 <u>18.5</u>	18.4	89.3 <u>85.9</u>	87.6	6.4 <u>6.1</u>	6.3		6.3	7.5 <u>7.8</u>		7.7	3.5 <u>4.1</u>		3.8			
28-May-14	Sunny	Moderate	13:32	3.1	Surface	1.0	28.2 <u>28.2</u>	28.2	8.6 <u>8.6</u>	8.6	16.8 <u>16.9</u>	16.9	119.7 <u>126.0</u>	122.9	8.5 <u>9.0</u>	8.7	8.7	6.5 <u>6.5</u>	6.5	6.6	6.3 <u>6.0</u>	6.2	6.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.1	27.6 <u>27.5</u>	27.5	8.4 <u>8.2</u>	8.3	18.9 <u>19.2</u>	19.1	111.6 <u>111.1</u>	111.4	7.9 <u>7.9</u>	7.9		7.9	6.6 <u>6.6</u>		6.6	6.3 <u>7.2</u>		6.8			
30-May-14	Sunny	Moderate	12:51	3.5	Surface	1.0	28.0 <u>28.2</u>	28.1	8.5 <u>8.5</u>	8.5	17.3 <u>17.1</u>	17.2	125.4 <u>125.5</u>	125.5	8.9 <u>8.9</u>	8.9	8.9	2.0 <u>1.9</u>	2.0	2.0	2.0 <u>3.0</u>	2.5	2.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.5	28.1 <u>27.9</u>	28.0	8.5 <u>8.5</u>	8.5	17.2 <u>17.3</u>	17.2	125.2 <u>124.4</u>	124.8	8.9 <u>8.9</u>	8.9		8.9	2.0 <u>2.0</u>		2.0	2.9 <u>2.9</u>		2.9			

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS7 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-May-14	Sunny	Moderate	08:18	3.5	Surface	1.0	23.9 23.9	23.9	8.4 8.4	8.4	26.4 26.4	26.4	88.4 88.7	88.6	6.4 6.4	6.4	6.4	4.9 4.5	4.7	5.0	3.8 4.3	4.1	4.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.5	23.9 23.9	23.9	8.4 8.4	8.4	26.6 26.6	26.6	88.3 88.9	88.6	6.4 6.4	6.4		6.4	5.4 5.2		5.3	6.4		5.4 5.2	5.3	4.5 3.6	4.1
5-May-14	Sunny	Moderate	09:52	3.3	Surface	1.0	24.2 24.2	24.2	8.4 8.4	8.4	26.6 26.6	26.6	96.8 98.0	97.4	7.0 7.1	7.0	7.0	1.9 2.0	2.0	2.0	2.5 3.2	2.9	3.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.3	24.2 24.2	24.2	8.4 8.4	8.4	26.7 26.7	26.7	97.2 99.4	98.3	7.0 7.2	7.1		7.1	2.0 2.0		2.0	7.1		2.0 2.0	2.0	2.9 3.0	3.0
7-May-14	Cloudy	Moderate	11:46	3.4	Surface	1.0	23.1 23.0	23.1	8.4 8.4	8.4	27.4 27.4	27.4	95.6 99.0	97.3	7.0 7.3	7.1	7.1	4.5 4.5	4.5	4.7	5.2 5.7	5.5	5.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.4	22.8 23.1	22.9	8.4 8.4	8.4	27.6 27.4	27.5	96.7 94.7	95.7	7.1 6.9	7.0		7.0	4.8 4.8		4.8	7.0		4.8 4.8	4.8	5.9 5.0	5.5
9-May-14	Rainy	Moderate	10:25	3.1	Surface	1.0	23.2 23.2	23.2	8.4 8.4	8.4	27.1 27.2	27.1	94.3 94.7	94.5	6.9 6.9	6.9	6.9	9.4 9.4	9.4	9.4	4.1 4.6	4.4	5.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.1	23.2 23.2	23.2	8.3 8.4	8.4	27.3 27.2	27.2	96.2 94.5	95.4	7.0 6.9	7.0		7.0	9.4 9.4		9.4	7.0		9.4 9.4	9.4	7.7 6.7	7.2
12-May-14	Sunny	Moderate	16:46	3.4	Surface	1.0	25.0 25.4	25.2	8.2 8.2	8.2	16.9 16.8	16.9	92.6 94.1	93.4	6.9 6.9	6.9	6.9	6.0 5.7	5.9	6.0	3.5 4.2	3.9	4.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.4	25.0 25.4	25.2	8.2 8.2	8.2	20.5 18.9	19.7	92.9 92.2	92.6	6.9 6.8	6.9		6.9	5.9 6.0		6.0	6.9		5.9 6.0	6.0	3.9 4.0	4.0
14-May-14	Sunny	Moderate	18:38	3.0	Surface	1.0	26.0 25.9	26.0	7.6 7.7	7.6	21.0 21.0	21.0	97.3 94.3	95.8	7.0 6.8	6.9	6.9	9.3 9.4	9.4	9.6	5.7 6.1	5.9	5.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.0	26.0 25.8	25.9	7.5 7.6	7.6	21.0 21.2	21.1	97.3 96.3	96.8	7.0 7.0	7.0		7.0	9.5 9.8		9.7	7.0		9.5 9.8	9.7	5.4 6.0	5.7
16-May-14	Cloudy	Moderate	07:38	3.2	Surface	1.0	25.7 25.7	25.7	7.6 7.6	7.6	18.4 17.9	18.2	91.4 91.3	91.4	6.7 6.7	6.7	6.7	5.2 5.0	5.1	5.4	6.6 6.1	6.4	6.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.2	25.7 25.7	25.7	7.6 7.6	7.6	18.3 18.7	18.5	86.4 84.8	85.6	6.4 6.2	6.3		6.3	5.6 5.7		5.7	6.3		5.6 5.7	5.7	6.2 5.7	6.0
19-May-14	Cloudy	Moderate	10:10	3.1	Surface	1.0	26.4 26.4	26.4	7.6 7.6	7.6	16.9 17.5	17.2	88.3 88.1	88.2	6.5 6.4	6.4	6.4	3.3 3.1	3.2	3.3	3.2 3.0	3.1	3.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.1	26.4 26.4	26.4	7.5 7.6	7.6	16.6 17.5	17.0	90.6 87.9	89.3	6.7 6.4	6.5		6.5	3.2 3.3		3.3	6.5		3.2 3.3	3.3	4.3 3.9	4.1
21-May-14	Cloudy	Moderate	11:54	3.2	Surface	1.0	26.6 26.7	26.7	7.6 7.6	7.6	14.9 14.9	14.9	90.5 90.1	90.3	6.7 6.6	6.7	6.7	3.5 3.3	3.4	3.5	4.0 3.8	3.9	3.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.2	26.4 26.5	26.5	7.6 7.6	7.6	14.9 14.9	14.9	90.9 89.8	90.4	6.7 6.6	6.7		6.7	3.4 3.5		3.5	6.7		3.4 3.5	3.5	2.0 4.0	3.0

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS7 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	13:34	3.2	Surface	1.0	26.5 <u>26.5</u>	26.5	7.5 <u>7.6</u>	7.6	17.1 <u>17.4</u>	17.2	81.7 <u>79.0</u>	80.4	6.0 <u>5.8</u>	5.9	5.9	9.5 <u>10.1</u>	9.8	10.1	3.3 <u>2.6</u>	3.0	3.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.2	26.4 <u>26.5</u>	26.4	7.5 <u>7.6</u>	7.5	17.9 <u>17.8</u>	17.8	86.0 <u>79.8</u>	82.9	6.3 <u>5.8</u>	6.0		6.0	10.1 <u>10.6</u>		10.4	6.0		10.1 <u>10.6</u>	10.4	6.0	2.8 <u>3.8</u>
26-May-14	Sunny	Moderate	17:31	3.1	Surface	1.0	29.1 <u>29.1</u>	29.1	7.8 <u>7.8</u>	7.8	14.2 <u>14.2</u>	14.2	119.3 <u>107.5</u>	113.4	8.5 <u>7.6</u>	8.1	8.1	4.0 <u>3.6</u>	3.8	3.9	2.8 <u>2.6</u>	2.7	3.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.1	28.7 <u>27.9</u>	28.3	7.8 <u>7.6</u>	7.7	16.0 <u>17.9</u>	17.0	119.5 <u>107.4</u>	113.5	8.5 <u>7.6</u>	8.0		8.0	4.0 <u>4.0</u>		4.0	8.0		4.0 <u>4.0</u>	4.0	8.0	3.0 <u>4.5</u>
28-May-14	Sunny	Moderate	18:54	3.0	Surface	1.0	29.1 <u>29.0</u>	29.1	8.7 <u>8.7</u>	8.7	17.2 <u>17.2</u>	17.2	160.2 <u>148.8</u>	154.5	10.9 <u>10.1</u>	10.5	10.5	8.1 <u>8.5</u>	8.3	8.6	8.4 <u>8.3</u>	8.4	8.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.0	29.0 <u>28.8</u>	28.9	8.7 <u>8.7</u>	8.7	17.5 <u>17.7</u>	17.6	151.8 <u>147.3</u>	149.6	10.3 <u>10.0</u>	10.1		10.1	8.9 <u>8.8</u>		8.9	10.1		8.9 <u>8.8</u>	8.9	10.1	9.4 <u>7.9</u>
30-May-14	Sunny	Moderate	07:17	3.4	Surface	1.0	27.7 <u>27.6</u>	27.6	8.3 <u>8.4</u>	8.3	16.1 <u>16.2</u>	16.1	104.3 <u>102.2</u>	103.3	7.5 <u>7.4</u>	7.4	7.4	1.5 <u>1.5</u>	1.5	1.6	3.7 <u>4.1</u>	3.9	3.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.4	27.6 <u>27.6</u>	27.6	8.4 <u>8.4</u>	8.4	16.5 <u>16.3</u>	16.4	100.7 <u>101.3</u>	101.0	7.3 <u>7.3</u>	7.3		7.3	1.7 <u>1.6</u>		1.7	7.3		1.7 <u>1.6</u>	1.7	7.3	3.8 <u>3.8</u>

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS8 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-May-14	Sunny	Moderate	14:33	3.5	Surface	1.0	24.6 24.6	24.6	8.3 8.3	8.3	26.3 26.3	26.3	92.0 91.7	91.9	6.6 6.6	6.6	6.6	2.6 2.8	2.7	3.2	5.0 3.9	4.5	4.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.5	24.2 24.2	24.2	8.2 8.3	8.3	26.7 26.7	26.7	90.0 90.2	90.1	6.5 6.5	6.5		3.6 3.7	3.7		6.5	3.6 3.7		3.7	3.8 4.8	4.3
5-May-14	Sunny	Moderate	16:26	3.7	Surface	1.0	24.2 24.2	24.2	8.3 8.4	8.4	26.8 26.7	26.7	94.3 95.0	94.7	6.8 6.8	6.8	6.8	2.7 2.7	2.7	3.1	3.8 3.4	3.6	3.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.7	24.3 24.2	24.3	8.3 8.4	8.3	27.9 27.7	27.8	94.4 94.9	94.7	6.7 6.8	6.8		3.6 3.3	3.5		6.8	3.6 3.3		3.5	3.6 4.6	4.1
7-May-14	Cloudy	Moderate	17:55	3.5	Surface	1.0	23.4 23.3	23.4	8.4 8.4	8.4	28.5 28.4	28.5	94.9 98.4	96.7	6.9 7.1	7.0	7.0	3.0 3.0	3.0	3.1	5.5 5.3	5.4	5.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.5	23.4 23.3	23.3	8.4 8.4	8.4	28.8 28.5	28.6	95.4 93.9	94.7	6.9 6.8	6.9		3.0 3.1	3.1		6.9	3.0 3.1		3.1	5.2 6.2	5.7
9-May-14	Rainy	Moderate	14:27	4.2	Surface	1.0	23.5 23.4	23.4	8.3 8.3	8.3	28.1 28.0	28.1	85.1 85.4	85.3	6.2 6.2	6.2	6.2	12.3 12.3	12.3	12.2	6.8 7.6	7.2	7.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.2	23.6 23.5	23.5	8.3 8.3	8.3	29.6 29.7	29.6	86.5 85.9	86.2	6.2 6.2	6.2		12.2 11.7	12.0		6.2	12.2 11.7		12.0	7.2 7.2	7.2
12-May-14	Sunny	Moderate	11:53	3.6	Surface	1.0	23.9 24.1	24.0	8.2 8.2	8.2	17.2 16.7	17.0	92.1 97.7	94.9	7.0 7.3	7.2	7.2	5.2 5.1	5.2	5.3	5.1 4.4	4.8	5.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.6	24.0 24.0	24.0	8.2 8.2	8.2	20.2 19.2	19.7	93.2 91.5	92.4	7.1 7.0	7.0		5.3 5.3	5.3		7.0	5.3 5.3		5.3	4.6 5.6	5.1
14-May-14	Sunny	Moderate	13:13	3.9	Surface	1.0	25.1 25.0	25.1	7.7 7.7	7.7	20.9 21.0	21.0	86.1 85.5	85.8	6.3 6.3	6.3	6.3	6.8 6.7	6.8	7.2	3.8 4.3	4.1	3.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.9	24.9 24.9	24.9	7.7 7.7	7.7	21.4 21.4	21.4	86.2 85.7	86.0	6.3 6.3	6.3		7.6 7.4	7.5		6.3	7.6 7.4		7.5	2.9 4.3	3.6
16-May-14	Cloudy	Moderate	13:40	3.8	Surface	1.0	26.2 26.2	26.2	7.7 7.7	7.7	19.1 19.1	19.1	94.1 93.7	93.9	6.8 6.8	6.8	6.8	7.2 7.2	7.2	7.2	3.2 3.4	3.3	3.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.8	26.2 26.1	26.1	7.7 7.6	7.6	20.3 20.2	20.3	94.0 95.0	94.5	6.8 6.9	6.8		7.1 7.2	7.2		6.8	7.1 7.2		7.2	3.2 4.4	3.8
19-May-14	Sunny	Rough	15:48	3.8	Surface	1.0	26.9 26.9	26.9	7.5 7.5	7.5	16.3 16.3	16.3	87.9 87.9	87.9	6.4 6.4	6.4	6.4	3.6 3.5	3.6	3.5	4.9 5.5	5.2	5.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.8	26.6 26.5	26.6	7.5 7.5	7.5	17.4 17.2	17.3	87.3 90.2	88.8	6.4 6.6	6.5		3.4 3.3	3.4		6.5	3.4 3.3		3.4	5.2 5.5	5.4
21-May-14	Cloudy	Moderate	17:46	3.9	Surface	1.0	26.6 26.6	26.6	7.6 7.6	7.6	16.0 16.1	16.0	83.2 81.8	82.5	6.1 6.0	6.1	6.1	5.8 5.7	5.8	5.8	4.6 5.1	4.9	5.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.9	26.5 26.1	26.3	7.5 7.6	7.6	17.5 18.6	18.1	83.2 81.9	82.6	6.1 6.0	6.0		5.7 5.8	5.8		6.0	5.7 5.8		5.8	3.9 6.1	5.0

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS8 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	09:14	3.7	Surface	1.0	<u>26.5</u> <u>26.6</u>	26.5	<u>7.7</u> <u>7.7</u>	7.7	13.9 15.2	14.5	80.4 82.5	81.5	6.0 6.1	6.0	6.0	3.6 3.5	3.6	4.5	2.9 2.6	2.8	2.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	<u>26.3</u> <u>26.3</u>	26.3	<u>7.6</u> <u>7.6</u>	7.6	18.6 18.8	18.7	82.3 81.0	81.7	6.0 5.9	5.9		5.3 5.5	5.4		5.3	5.4		2.7 2.2	2.5		
26-May-14	Sunny	Moderate	11:55	3.7	Surface	1.0	<u>28.0</u> <u>27.9</u>	28.0	<u>7.6</u> <u>7.6</u>	7.6	13.3 13.5	13.4	99.4 96.2	97.8	7.2 7.0	7.1	7.1	2.0 2.2	2.1	2.2	3.4 3.1	3.3	3.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.7	<u>27.9</u> <u>27.9</u>	27.9	<u>7.6</u> <u>7.6</u>	7.6	15.0 15.3	15.1	98.6 93.6	96.1	7.1 6.8	6.9		2.1 2.3	2.2		2.1	2.2		3.3 3.3	3.3		
28-May-14	Sunny	Moderate	13:02	3.9	Surface	1.0	<u>28.2</u> <u>28.5</u>	28.3	<u>8.5</u> <u>8.5</u>	8.5	17.8 17.4	17.6	118.0 116.2	117.1	8.3 8.2	8.3	8.3	4.6 4.6	4.6	4.6	6.4 5.6	6.0	6.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.9	<u>26.8</u> <u>26.8</u>	26.8	<u>8.1</u> <u>8.1</u>	8.1	20.2 19.1	19.7	92.1 94.5	93.3	6.7 6.8	6.7		4.6 4.6	4.6		4.6	4.6		7.0 7.4	7.2		
30-May-14	Sunny	Moderate	13:13	3.3	Surface	1.0	<u>28.7</u> <u>28.3</u>	28.5	<u>8.6</u> <u>8.6</u>	8.6	17.1 18.4	17.7	124.2 130.4	127.3	8.7 9.2	9.0	9.0	1.9 1.9	1.9	2.0	3.7 3.3	3.5	4.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.3	<u>28.7</u> <u>28.6</u>	28.6	<u>8.6</u> <u>8.6</u>	8.6	18.3 18.5	18.4	103.1 127.3	115.2	7.2 8.9	8.1		2.1 2.1	2.1		2.1	2.1		5.2 4.8	5.0		

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS8 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-May-14	Sunny	Moderate	07:50	3.6	Surface	1.0	23.9 23.9	23.9	8.4 8.4	8.4	26.6 26.6	26.6	85.1 85.2	85.2	6.2 6.2	6.2	6.2	6.2 5.9	6.1	6.4	5.1 4.6	4.9	4.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	23.9 23.9	23.9	8.4 8.4	8.4	27.1 27.1	27.1	84.6 84.7	84.7	6.1 6.1	6.1		6.1	6.5 6.9		6.7	6.1		6.5 6.9	6.7	4.7 3.9	4.3
5-May-14	Sunny	Moderate	09:28	3.7	Surface	1.0	24.2 24.2	24.2	8.4 8.4	8.4	24.8 24.8	24.8	92.7 94.6	93.7	6.7 6.9	6.8	6.8	3.8 4.1	4.0	4.5	3.6 3.4	3.5	3.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	24.1 24.2	24.1	8.4 8.4	8.4	25.5 25.5	25.5	96.5 93.0	94.8	7.0 6.8	6.9		6.9	5.2 4.8		5.0	6.9		5.2 4.8	5.0	2.9 2.9	2.9
7-May-14	Cloudy	Moderate	11:24	3.5	Surface	1.0	23.5 23.5	23.5	8.4 8.4	8.4	28.9 28.9	28.9	96.9 92.7	94.8	7.0 6.7	6.8	6.8	4.0 3.8	3.9	4.1	5.5 6.0	5.8	5.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.5	23.4 23.5	23.5	8.4 8.4	8.4	28.9 29.0	29.0	92.0 93.7	92.9	6.6 6.8	6.7		6.7	4.2 4.2		4.2	6.7		4.2 4.2	4.2	6.1 5.3	5.7
9-May-14	Rainy	Moderate	10:03	4.1	Surface	1.0	23.3 23.3	23.3	8.4 8.4	8.4	28.0 27.9	28.0	92.1 93.2	92.7	6.7 6.8	6.7	6.7	9.5 9.5	9.5	9.6	13.7 15.5	14.6	15.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	23.4 23.3	23.4	8.3 8.4	8.3	28.5 28.4	28.5	95.3 92.8	94.1	6.9 6.7	6.8		6.8	9.6 9.5		9.6	6.8		9.6 9.5	9.6	16.3 15.3	15.8
12-May-14	Sunny	Moderate	17:08	3.5	Surface	1.0	25.1 24.9	25.0	8.1 8.1	8.1	17.1 17.5	17.3	94.0 90.8	92.4	7.0 6.8	6.9	6.9	5.2 5.2	5.2	5.3	4.9 4.4	4.7	4.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.5	25.0 24.5	24.7	8.1 8.2	8.2	17.5 19.0	18.2	90.6 91.3	91.0	6.8 6.8	6.8		6.8	5.3 5.4		5.4	6.8		5.3 5.4	5.4	3.9 3.9	3.9
14-May-14	Sunny	Moderate	19:01	4.2	Surface	1.0	25.0 25.1	25.1	7.6 7.6	7.6	21.8 21.7	21.7	81.1 80.8	81.0	5.9 5.9	5.9	5.9	16.4 16.5	16.5	16.7	4.9 4.9	4.9	5.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.2	24.8 24.9	24.9	7.6 7.6	7.6	22.4 22.2	22.3	83.3 80.6	82.0	6.1 5.9	6.0		6.0	16.5 17.2		16.9	6.0		16.5 17.2	16.9	5.2 5.1	5.2
16-May-14	Cloudy	Moderate	07:13	4.3	Surface	1.0	25.4 25.5	25.4	7.6 7.6	7.6	17.7 17.7	17.7	80.0 79.7	79.9	5.9 5.9	5.9	5.9	7.3 7.1	7.2	7.4	5.9 4.9	5.4	5.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.3	25.4 25.4	25.4	7.6 7.6	7.6	18.6 18.9	18.7	79.5 80.9	80.2	5.9 6.0	5.9		5.9	7.6 7.4		7.5	5.9		7.6 7.4	7.5	6.2 5.2	5.7
19-May-14	Cloudy	Moderate	09:41	3.9	Surface	1.0	26.0 26.0	26.0	7.5 7.5	7.5	15.1 15.4	15.3	74.1 75.4	74.8	5.5 5.6	5.6	5.6	4.7 4.7	4.7	4.8	6.9 6.1	6.5	6.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.9	25.9 26.0	26.0	7.5 7.5	7.5	16.5 16.6	16.6	74.6 77.2	75.9	5.5 5.7	5.6		5.6	4.8 4.8		4.8	5.6		4.8 4.8	4.8	7.2 7.1	7.2
21-May-14	Cloudy	Moderate	11:30	4.1	Surface	1.0	26.2 26.2	26.2	7.6 7.5	7.6	15.0 15.5	15.3	77.3 79.0	78.2	5.7 5.9	5.8	5.8	8.4 8.8	8.6	8.7	7.0 5.7	6.4	6.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	26.2 26.3	26.3	7.6 7.5	7.5	15.8 16.0	15.9	77.8 81.3	79.6	5.8 6.0	5.9		5.9	8.7 8.7		8.7	5.9		8.7 8.7	8.7	6.4 5.1	5.8

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS8 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	13:56	3.5	Surface	1.0	26.5 26.5	26.5	7.6 7.6	7.6	15.1 14.6	14.9	89.1 89.3	89.2	6.6 6.6	6.6	6.6	3.2 3.4	3.3	3.4	3.4 3.5	3.5	3.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.5	26.5 26.5	26.5	7.6 7.6	7.6	15.5 15.5	15.5	89.0 88.7	88.9	6.6 6.5	6.5		6.5	3.6 3.4		3.5	6.5		3.6 3.3	3.5	6.5	2.1 2.7
26-May-14	Sunny	Moderate	17:58	3.5	Surface	1.0	28.1 27.9	28.0	7.6 7.7	7.7	12.5 12.4	12.5	97.6 97.1	97.4	7.1 7.1	7.1	7.1	5.7 6.0	5.9	7.9	3.8 4.2	4.0	5.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.5	27.8 27.7	27.8	7.6 7.5	7.6	16.4 17.3	16.9	97.7 95.6	96.7	7.0 6.8	6.9		6.9	9.6 10.1		9.9	6.9		9.6 10.1	9.9	6.9	5.8 6.2
28-May-14	Sunny	Moderate	19:19	3.9	Surface	1.0	28.6 28.6	28.6	8.6 8.6	8.6	16.9 16.9	16.9	141.3 143.2	142.3	10.0 10.1	10.0	10.0	7.6 7.7	7.7	8.2	5.4 6.0	5.7	6.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.9	27.4 27.7	27.5	8.3 8.5	8.4	19.4 18.7	19.0	124.1 128.5	126.3	8.8 9.1	9.0		9.0	8.6 8.7		8.7	9.0		8.6 8.7	8.7	9.0	6.6 6.1
30-May-14	Sunny	Moderate	06:53	3.3	Surface	1.0	27.3 27.4	27.3	8.3 8.2	8.3	14.9 15.0	15.0	101.1 93.5	97.3	7.4 6.7	7.1	7.1	1.5 1.6	1.6	1.6	3.3 3.9	3.6	3.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.3	26.9 27.4	27.1	8.4 8.3	8.3	15.9 17.4	16.7	97.0 90.0	93.5	7.1 6.6	6.8		6.8	1.6 1.6		1.6	6.8		1.6 1.6	1.6	6.8	3.1 3.5

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS17 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	14:47	10.6	Surface	1.0	24.5 24.5	24.5	8.3 8.3	8.3	26.7 26.8	26.7	89.6 89.4	89.5	6.4 6.4	6.4	6.4	5.5 5.4	5.5	5.9	4.9 5.6	5.3	4.6
					Middle	5.3	24.3 24.3	24.3	8.3 8.3	8.3	27.3 27.3	27.3	87.6 87.4	87.5	6.3 6.3	6.3		6.3 6.0	6.2		4.1 4.6	4.4	
					Bottom	9.6	24.0 24.1	24.0	8.3 8.3	8.3	28.1 28.0	28.0	87.2 86.9	87.1	6.3 6.2	6.2		6.5 5.6	6.1		4.0 4.1	4.1	
5-May-14	Sunny	Moderate	16:44	11.5	Surface	1.0	24.1 24.1	24.1	8.4 8.4	8.4	26.8 26.2	26.5	89.6 90.1	89.9	6.5 6.5	6.5	6.4	3.9 3.9	3.9	4.3	4.2 2.9	3.6	3.3
					Middle	5.8	23.9 24.0	23.9	8.4 8.4	8.4	30.6 30.5	30.6	89.6 88.9	89.3	6.3 6.3	6.3		4.5 4.4	4.5		3.0 2.9	3.0	
					Bottom	10.5	23.9 24.0	23.9	8.4 8.4	8.4	31.1 31.2	31.2	91.5 90.4	91.0	6.5 6.4	6.4		4.6 4.3	4.5		3.1 3.7	3.4	
7-May-14	Cloudy	Moderate	18:10	11.1	Surface	1.0	23.5 23.6	23.5	8.4 8.4	8.4	29.7 29.5	29.6	88.9 87.3	88.1	6.4 6.3	6.3	6.3	4.6 4.7	4.7	4.9	6.3 7.0	6.7	6.0
					Middle	5.6	23.7 23.7	23.7	8.4 8.4	8.4	31.1 30.5	30.8	87.8 87.2	87.5	6.2 6.2	6.2		5.0 5.0	5.0		5.8 6.0	5.9	
					Bottom	10.1	23.7 23.7	23.7	8.4 8.4	8.4	31.5 31.3	31.4	86.4 86.9	86.7	6.1 6.2	6.2		5.1 5.1	5.1		5.4 5.5	5.5	
9-May-14	Rainy	Moderate	14:45	10.8	Surface	1.0	23.5 23.5	23.5	8.4 8.4	8.4	29.4 29.4	29.4	89.7 89.6	89.7	6.4 6.4	6.4	6.4	4.4 4.4	4.4	4.6	7.8 8.7	8.3	12.8
					Middle	5.4	23.5 23.5	23.5	8.4 8.4	8.4	29.5 29.5	29.5	88.6 88.7	88.7	6.4 6.4	6.4		4.4 4.5	4.5		14.4 14.6	14.5	
					Bottom	9.8	23.5 23.6	23.6	8.4 8.3	8.3	29.8 30.3	30.1	89.6 90.2	89.9	6.4 6.4	6.4		4.8 4.8	4.8		15.9 15.2	15.6	
12-May-14	Sunny	Moderate	11:39	11.3	Surface	1.0	23.8 23.9	23.9	8.2 8.2	8.2	16.3 16.5	16.4	90.1 85.8	88.0	6.6 6.6	6.6	6.5	5.5 5.6	5.6	5.7	5.2 3.9	4.6	4.4
					Middle	5.7	23.8 23.7	23.7	8.2 8.2	8.2	21.7 23.7	22.7	85.9 85.2	85.6	6.5 6.2	6.3		5.8 5.6	5.7		4.2 3.9	4.1	
					Bottom	10.3	23.8 23.7	23.8	8.2 8.2	8.2	27.7 27.5	27.6	85.8 83.1	84.5	6.4 6.2	6.3		5.8 5.8	5.8		4.1 4.7	4.4	
14-May-14	Sunny	Moderate	13:00	9.9	Surface	1.0	24.7 25.0	24.8	7.7 7.7	7.7	21.3 21.2	21.2	83.5 86.0	84.8	6.1 6.3	6.2	6.2	7.6 7.8	7.7	7.8	6.9 6.8	6.9	7.3
					Middle	5.0	24.6 24.7	24.7	7.7 7.6	7.7	21.3 21.4	21.4	83.6 84.6	84.1	6.2 6.2	6.2		7.6 7.8	7.7		7.6 7.3	7.5	
					Bottom	8.9	24.5 24.6	24.6	7.6 7.6	7.6	21.8 24.2	23.0	85.1 84.5	84.8	6.3 6.1	6.2		7.8 8.2	8.0		7.3 7.6	7.5	
16-May-14	Cloudy	Moderate	14:14	10.1	Surface	1.0	25.7 25.6	25.6	7.7 7.7	7.7	20.2 20.4	20.3	85.0 83.5	84.3	6.2 6.1	6.1	6.1	11.3 11.5	11.4	11.3	8.4 8.3	8.4	8.7
					Middle	5.1	25.3 25.0	25.2	7.7 7.7	7.7	21.0 22.7	21.8	82.5 81.6	82.1	6.0 5.9	6.0		11.6 11.1	11.4		8.2 9.6	8.9	
					Bottom	9.1	24.6 24.9	24.8	7.7 7.7	7.7	26.2 26.0	26.1	82.1 82.6	82.4	5.9 5.9	5.9		11.2 11.2	11.2		8.5 9.0	8.8	
19-May-14	Sunny	Rough	16:01	9.9	Surface	1.0	26.7 26.7	26.7	7.5 7.5	7.5	16.9 17.1	17.0	84.9 84.8	84.9	6.2 6.2	6.2	6.1	6.2 6.2	6.2	7.5	5.8 6.1	6.0	7.9
					Middle	5.0	26.0 26.0	26.0	7.6 7.5	7.6	18.7 18.8	18.7	81.4 81.2	81.3	5.9 5.9	5.9		8.0 8.2	8.1		8.7 9.0	8.9	
					Bottom	8.9	25.3 25.3	25.3	7.5 7.5	7.5	23.8 24.2	24.0	82.4 82.1	82.3	5.9 5.9	5.9		8.1 8.4	8.3		8.9 8.8	8.9	
21-May-14	Cloudy	Moderate	18:00	10.2	Surface	1.0	26.6 26.4	26.5	7.6 7.6	7.6	15.9 15.7	15.8	81.5 78.5	80.0	6.0 5.8	5.9	5.7	5.7 5.7	5.7	5.7	4.3 3.5	3.9	4.4
					Middle	5.1	25.4 25.6	25.5	7.7 7.6	7.7	22.8 21.9	22.4	76.1 76.8	76.5	5.5 5.5	5.5		5.7 5.8	5.8		4.4 4.1	4.3	
					Bottom	9.2	25.3 25.4	25.4	7.7 7.6	7.6	25.9 26.5	26.2	77.1 77.8	77.5	5.5 5.5	5.5		5.5 5.6	5.6		4.6 5.6	5.1	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS17 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	09:00	10.9	Surface	1.0	26.1 26.3	26.2	7.7 7.6	7.6	14.2 14.0	14.1	79.8 79.8	79.8	6.0 6.0	6.0	5.8	3.6 3.6	3.6	3.6	3.4 2.7	3.1	3.3
					Middle	5.5	25.6 25.4	25.5	7.7 7.6	7.7	23.5 24.3	23.9	77.4 79.5	78.5	5.5 5.7	5.6		3.4 3.3	3.4		3.3 3.0	3.2	
					Bottom	9.9	25.7 25.4	25.6	7.6 7.6	7.6	24.7 25.5	25.1	79.0 84.0	81.5	5.6 6.0	5.8		3.8 3.7	3.8		3.9 3.0	3.5	
26-May-14	Sunny	Moderate	11:41	10.3	Surface	1.0	27.7 27.8	27.8	7.5 7.5	7.5	12.1 12.6	12.3	83.3 89.1	86.2	6.1 6.5	6.3	5.9	5.0 4.5	4.8	5.1	3.1 3.0	3.1	4.3
					Middle	5.2	26.9 26.3	26.6	7.5 7.5	7.5	16.1 19.2	17.7	76.4 74.4	75.4	5.6 5.4	5.5		5.0 5.6	5.3		3.8 4.2	4.0	
					Bottom	9.3	26.2 26.3	26.2	7.5 7.4	7.5	20.4 19.2	19.8	71.6 76.4	74.0	5.2 5.5	5.4		5.3 5.2	5.3		5.5 6.1	5.8	
28-May-14	Sunny	Moderate	12:47	9.9	Surface	1.0	28.8 28.8	28.8	8.5 8.5	8.5	16.1 16.2	16.1	123.6 118.9	121.3	8.7 8.4	8.6	7.0	3.6 3.6	3.6	3.6	3.9 3.9	3.9	4.0
					Middle	5.0	26.8 26.6	26.7	8.1 8.1	8.1	20.3 20.9	20.6	77.0 74.9	76.0	5.5 5.3	5.4		3.6 3.6	3.6		3.8 4.3	4.1	
					Bottom	8.9	26.3 26.0	26.1	8.0 8.1	8.1	23.9 25.1	24.5	77.3 76.6	77.0	5.5 5.4	5.4		3.6 3.5	3.6		4.1 4.0	4.1	
30-May-14	Sunny	Moderate	13:27	10.9	Surface	1.0	27.2 27.4	27.3	8.3 8.3	8.3	17.2 17.3	17.3	80.5 79.1	79.8	5.5 5.7	5.6	5.5	2.9 2.8	2.9	3.1	5.8 6.0	5.9	5.7
					Middle	5.5	26.4 26.2	26.3	8.2 8.2	8.2	24.7 25.2	24.9	77.6 75.6	76.6	5.6 5.2	5.4		3.0 3.1	3.1		6.2 4.9	5.6	
					Bottom	9.9	26.1 26.7	26.4	8.2 8.2	8.2	27.7 27.5	27.6	73.3 76.1	74.7	5.1 5.3	5.2		3.2 3.1	3.2		5.3 5.9	5.6	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS17 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	07:37	10.9	Surface	1.0	24.0 24.0	24.0	8.4 8.4	8.4	25.9 26.2	26.1	86.9 87.1	87.0	6.3 6.3	6.3	6.3	3.8 4.0	3.9	4.3	2.6 2.8	2.7	3.4
					Middle	5.5	23.9 23.9	23.9	8.4 8.4	8.4	27.2 27.4	27.3	86.8 86.7	86.8	6.3 6.2	6.3	4.4 4.2	4.3	3.0 3.2		3.1		
					Bottom	9.9	23.9 23.9	23.9	8.4 8.4	8.4	28.2 27.9	28.0	87.4 86.8	87.1	6.3 6.2	6.3	4.9 4.6	4.8	4.0 4.9		4.5		
5-May-14	Sunny	Moderate	09:15	11.3	Surface	1.0	24.2 24.2	24.2	8.4 8.4	8.4	24.5 24.6	24.5	90.9 92.4	91.7	6.6 6.7	6.7	6.7	2.5 2.5	2.5	2.6	4.3 4.7	4.5	4.2
					Middle	5.7	24.1 24.1	24.1	8.4 8.4	8.4	28.0 28.0	28.0	93.3 90.6	92.0	6.7 6.5	6.6	2.7 2.4	2.6	4.1 4.2		4.2		
					Bottom	10.3	24.1 24.1	24.1	8.4 8.4	8.4	28.0 28.1	28.0	95.9 91.0	93.5	6.9 6.5	6.7	2.8 2.5	2.7	4.8 3.1		4.0		
7-May-14	Cloudy	Moderate	11:11	11.4	Surface	1.0	23.6 23.5	23.5	8.4 8.4	8.4	29.5 29.5	29.5	94.3 89.0	91.7	6.7 6.4	6.5	6.4	4.6 4.5	4.6	5.0	4.0 4.2	4.1	4.9
					Middle	5.7	23.8 23.8	23.8	8.4 8.4	8.4	31.1 30.9	31.0	86.9 88.9	87.9	6.1 6.3	6.2	5.0 5.1	5.1	4.8 4.6		4.7		
					Bottom	10.4	23.8 23.7	23.8	8.4 8.4	8.4	31.4 31.3	31.3	85.7 88.3	87.0	6.3 6.3	6.2	5.1 5.3	5.2	5.4 6.3		5.9		
9-May-14	Rainy	Moderate	09:43	10.1	Surface	1.0	23.6 23.6	23.6	8.4 8.4	8.4	29.8 29.8	29.8	85.8 85.2	85.5	6.1 6.1	6.1	6.1	9.1 9.2	9.2	11.9	7.0 8.4	7.7	8.7
					Middle	5.1	23.6 23.6	23.6	8.4 8.4	8.4	30.2 30.2	30.2	84.7 85.1	84.9	6.0 6.1	6.0	13.5 13.1	13.3	7.9 6.4		7.2		
					Bottom	9.1	23.6 23.6	23.6	8.4 8.4	8.4	30.4 30.6	30.5	85.4 86.0	85.7	6.1 6.1	6.1	13.1 13.2	13.2	11.8 10.8		11.3		
12-May-14	Sunny	Moderate	17:23	11.5	Surface	1.0	24.3 24.2	24.3	8.1 8.2	8.2	17.7 17.7	17.7	86.5 84.3	85.4	6.6 6.4	6.5	6.3	6.5 6.3	6.4	6.6	5.3 5.7	5.5	5.3
					Middle	5.8	23.7 23.9	23.8	8.2 8.2	8.2	22.9 22.8	22.8	80.5 83.6	82.1	5.9 6.1	6.0	6.6 6.6	6.6	5.3 5.2		5.3		
					Bottom	10.5	23.8 23.7	23.7	8.2 8.2	8.2	27.2 27.2	27.2	82.2 79.9	81.1	6.1 5.8	5.9	6.6 6.8	6.7	5.8 4.1		5.0		
14-May-14	Sunny	Moderate	19:16	10.3	Surface	1.0	25.5 25.4	25.5	7.6 7.6	7.6	19.0 18.7	18.9	88.6 86.1	87.4	6.5 6.2	6.4	6.4	7.8 7.7	7.8	7.6	6.9 7.2	7.1	6.4
					Middle	5.2	25.0 24.8	24.9	7.6 7.6	7.6	21.2 21.4	21.3	85.9 87.6	86.8	6.3 6.4	6.4	7.5 7.3	7.4	6.2 5.6		5.9		
					Bottom	9.3	24.8 24.9	24.9	7.6 7.7	7.6	22.3 23.9	23.1	87.2 84.4	85.8	6.4 6.2	6.3	7.5 7.5	7.5	6.2 5.9		6.1		
16-May-14	Cloudy	Moderate	06:58	10.5	Surface	1.0	25.4 25.2	25.3	7.7 7.7	7.7	17.6 18.6	18.1	81.0 81.2	81.1	6.0 6.0	6.0	6.0	6.8 7.0	6.9	9.2	6.0 6.2	6.1	6.8
					Middle	5.3	25.1 25.0	25.0	7.7 7.7	7.7	21.0 22.3	21.6	80.5 81.1	80.8	5.9 5.9	5.9	10.3 10.7	10.5	6.2 7.4		6.8		
					Bottom	9.5	24.8 25.0	24.9	7.7 7.7	7.7	23.9 23.7	23.8	80.9 79.9	80.4	5.9 5.8	5.8	10.1 10.3	10.2	7.3 7.5		7.4		
19-May-14	Cloudy	Moderate	09:24	10.5	Surface	1.0	25.9 25.8	25.9	7.6 7.6	7.6	15.9 16.0	16.0	75.8 76.6	76.2	5.6 5.7	5.7	5.7	4.7 4.8	4.8	4.8	7.1 6.6	6.9	7.2
					Middle	5.3	25.5 25.6	25.5	7.6 7.7	7.6	20.1 19.8	20.0	76.9 75.8	76.4	5.6 5.5	5.6	4.7 4.8	4.8	7.4 6.8		7.1		
					Bottom	9.5	25.3 25.3	25.3	7.7 7.6	7.7	23.2 23.9	23.5	75.8 78.1	77.0	5.5 5.6	5.5	4.7 4.8	4.8	7.4 7.9		7.7		
21-May-14	Cloudy	Moderate	11:16	10.9	Surface	1.0	26.3 26.1	26.2	7.6 7.7	7.6	14.9 15.3	15.1	79.7 76.3	78.0	5.9 5.7	5.8	5.7	4.4 4.3	4.4	4.5	5.9 4.2	5.1	5.6
					Middle	5.5	25.9 25.7	25.8	7.6 7.7	7.7	16.8 17.1	16.9	76.3 75.6	76.0	5.6 5.6	5.6	4.4 4.5	4.5	4.9 5.3		5.1		
					Bottom	9.9	25.4 25.6	25.5	7.6 7.6	7.6	24.1 25.8	25.0	77.5 76.2	76.9	5.6 5.4	5.5	4.4 4.5	4.5	6.7 6.3		6.5		

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at IS17 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	14:14	10.9	Surface	1.0	26.3 26.3	26.3	7.6 7.6	7.6	14.7 14.7	14.7	79.6 78.5	79.1	5.9 5.8	5.9	5.8	3.6 3.2	3.4	3.4	3.8 3.2	3.5	3.1
					Middle	5.5	26.0 25.9	25.9	7.6 7.6	7.6	17.9 18.5	18.2	76.5 76.2	76.4	5.6 5.6	5.6		3.4 3.5	3.5		2.8 3.8	3.3	
					Bottom	9.9	25.8 25.9	25.8	7.6 7.6	7.6	20.5 21.5	21.0	76.8 78.2	77.5	5.6 5.6	5.6		3.4 3.2	3.3		2.4 2.8	2.6	
26-May-14	Sunny	Moderate	18:15	10.6	Surface	1.0	28.4 28.4	28.4	7.7 7.7	7.7	12.8 12.9	12.9	92.9 100.0	96.5	6.7 7.2	7.0	6.2	3.5 3.5	3.5	4.1	3.6 3.8	3.7	3.9
					Middle	5.3	26.6 26.5	26.5	7.5 7.5	7.5	17.7 17.8	17.8	73.0 73.6	73.3	5.3 5.4	5.3		4.2 4.4	4.3		4.0 3.7	3.9	
					Bottom	9.6	26.2 25.9	26.1	7.5 7.5	7.5	21.2 22.1	21.6	79.5 79.2	79.4	5.7 5.7	5.7		4.4 4.8	4.6		4.2 3.9	4.1	
28-May-14	Sunny	Moderate	19:36	10.9	Surface	1.0	28.5 28.5	28.5	8.7 8.7	8.7	14.7 15.1	14.9	129.6 125.6	127.6	9.3 9.0	9.1	7.4	3.5 3.6	3.6	4.2	4.2 3.3	3.8	4.0
					Middle	5.5	26.8 26.7	26.8	8.3 8.2	8.3	19.9 20.3	20.1	79.9 81.1	80.5	5.7 5.7	5.7		4.5 4.2	4.4		3.7 3.2	3.5	
					Bottom	9.9	26.7 26.1	26.4	8.2 8.2	8.2	21.2 25.1	23.2	79.8 76.6	78.2	5.7 5.5	5.6		4.5 4.5	4.5		4.5 5.0	4.8	
30-May-14	Sunny	Moderate	06:39	11.0	Surface	1.0	27.4 27.0	27.2	8.3 8.2	8.3	16.8 16.7	16.8	90.1 82.8	86.5	6.5 5.8	6.1	5.8	2.5 2.4	2.5	2.7	5.4 4.8	5.1	4.6
					Middle	5.5	26.8 26.7	26.7	8.2 8.2	8.2	20.8 21.4	21.1	73.8 77.0	75.4	5.2 5.6	5.4		2.6 2.6	2.6		4.1 5.0	4.6	
					Bottom	10.0	26.3 26.2	26.3	8.2 8.2	8.2	26.0 26.0	26.0	76.0 73.4	74.7	5.4 5.2	5.3		2.8 2.9	2.9		4.4 3.7	4.1	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR3 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)						
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*			
2-May-14	Sunny	Moderate	13:40	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	24.3 24.4	24.4	8.2 8.2	8.2	27.8 27.7	27.7	92.1 92.0	92.1	6.6 6.6	6.6	6.6	6.6	6.6	3.5 3.4	3.5	3.5	4.6 4.1	4.4	4.4
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
5-May-14	Sunny	Moderate	15:26	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.8	24.4 24.4	24.4	8.5 8.5	8.5	28.1 28.2	28.2	96.4 95.4	95.9	6.9 6.8	6.8	6.8	6.8	6.8	3.6 3.5	3.6	3.6	4.9 6.1	5.5	5.5
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
7-May-14	Cloudy	Moderate	17:09	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	23.3 23.3	23.3	8.3 8.4	8.3	28.5 28.5	28.5	97.3 95.1	96.2	7.0 6.9	7.0	7.0	7.0	7.0	2.4 2.4	2.4	2.4	6.0 5.5	5.8	5.8
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
9-May-14	Rainy	Moderate	13:46	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	23.4 23.4	23.4	8.4 8.3	8.4	26.3 26.4	26.3	91.6 92.1	91.9	6.7 6.7	6.7	6.7	6.7	6.7	6.2 6.4	6.3	6.3	11.7 10.2	11.0	11.0
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
12-May-14	Sunny	Moderate	12:41	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.8	24.0 24.0	24.0	8.2 8.2	8.2	15.7 15.7	15.7	91.0 91.0	91.0	7.0 7.0	7.0	7.0	7.0	7.0	8.2 8.2	8.2	8.2	5.9 7.1	6.5	6.5
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
14-May-14	Sunny	Moderate	14:01	1.2	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.6	25.7 25.8	25.8	7.7 7.7	7.7	20.5 20.5	20.5	93.0 92.8	92.9	6.8 6.7	6.7	6.7	6.7	6.7	5.8 5.8	5.8	5.8	6.8 6.3	6.6	6.6
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
16-May-14	Cloudy	Moderate	12:45	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.8	25.8 25.8	25.8	7.6 7.6	7.6	20.9 20.8	20.9	91.6 89.9	90.8	6.6 6.5	6.6	6.6	6.6	6.6	12.2 12.0	12.1	12.1	7.2 7.4	7.3	7.3
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
19-May-14	Sunny	Rough	15:00	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	26.8 26.8	26.8	7.6 7.6	7.6	17.7 17.7	17.7	91.6 91.2	91.4	6.6 6.6	6.6	6.6	6.6	6.6	8.4 8.2	8.3	8.3	12.7 11.7	12.2	12.2
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
21-May-14	Cloudy	Moderate	17:01	1.2	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.6	26.9 26.9	26.9	7.5 7.5	7.5	16.1 16.2	16.1	90.5 89.8	90.2	6.6 6.6	6.6	6.6	6.6	6.6	5.8 5.5	5.7	5.7	5.8 6.0	5.9	5.9
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR3 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	10:10	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
					Middle	0.8	<u>26.5</u> <u>26.5</u>	26.5	<u>7.6</u> <u>7.6</u>	7.6	15.3 15.4	15.4	<u>84.3</u> <u>81.8</u>	83.1	6.2 6.0	6.1	6.1	3.7 4.0	3.9	3.9	2.8 3.5	3.2	3.2
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
26-May-14	Sunny	Moderate	12:52	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.8	<u>28.1</u> <u>28.0</u>	28.0	<u>7.7</u> <u>7.7</u>	7.7	13.7 13.9	13.8	<u>103.2</u> <u>103.1</u>	103.2	7.5 7.5	7.5	7.5	2.9 2.8	2.9	2.9	3.9 4.2	4.1	4.1
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
28-May-14	Sunny	Moderate	13:58	1.2	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.6	<u>28.7</u> <u>28.7</u>	28.7	<u>8.6</u> <u>8.6</u>	8.6	17.6 17.6	17.6	<u>141.5</u> <u>143.1</u>	142.3	9.9 10.1	10.0	10.0	3.4 3.5	3.5	3.5	7.2 7.3	7.3	7.3
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
30-May-14	Sunny	Moderate	12:30	1.2	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.6	<u>28.2</u> <u>28.2</u>	28.2	<u>8.5</u> <u>8.5</u>	8.5	19.5 19.5	19.5	<u>126.3</u> <u>124.1</u>	125.2	8.8 8.7	8.8	8.8	2.3 2.1	2.2	2.2	4.7 4.7	4.7	4.7
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR3 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-May-14	Sunny	Moderate	08:43	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			
					Middle	0.8	23.9 23.9	23.9	8.3 8.3	8.3	26.4 26.3	26.4	88.2 88.2	88.2	6.4 6.4	6.4	6.4	6.4	6.4	6.4	10.7 10.7	10.7	10.7	4.9 5.9	5.4	5.4
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
5-May-14	Sunny	Moderate	10:25	1.8	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.9	24.2 24.2	24.2	8.4 8.3	8.4	26.3 26.3	26.3	95.3 95.2	95.3	6.9 6.9	6.9	6.9	6.9	6.9	6.9	3.0 3.3	3.2	3.2	4.2 3.2	3.7	3.7
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
7-May-14	Cloudy	Moderate	12:10	1.8	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.9	23.1 23.1	23.1	8.3 8.3	8.3	27.7 27.7	27.7	91.9 91.9	91.9	6.7 6.7	6.7	6.7	6.7	6.7	6.7	2.5 2.4	2.5	2.5	6.3 7.3	6.8	6.8
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
9-May-14	Rainy	Moderate	10:47	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.8	23.4 23.4	23.4	8.4 8.3	8.4	26.3 26.3	26.3	90.9 90.6	90.8	6.7 6.6	6.6	6.6	6.6	6.6	6.6	6.4 6.2	6.3	6.3	6.8 6.0	6.4	6.4
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
12-May-14	Sunny	Moderate	16:24	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	25.3 25.2	25.2	8.2 8.1	8.1	16.7 16.7	16.7	94.4 93.7	94.1	7.1 7.0	7.0	7.0	7.0	7.0	7.0	4.8 4.8	4.8	4.8	5.2 4.2	4.7	4.7
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
14-May-14	Sunny	Moderate	18:15	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	25.6 25.5	25.6	7.6 7.6	7.6	22.3 22.4	22.3	90.3 89.0	89.7	6.5 6.4	6.5	6.5	6.5	6.5	6.5	6.6 6.4	6.5	6.5	5.8 5.4	5.6	5.6
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
16-May-14	Cloudy	Moderate	08:00	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	25.8 25.8	25.8	7.6 7.6	7.6	18.7 18.7	18.7	85.8 85.8	85.8	6.3 6.3	6.3	6.3	6.3	6.3	6.3	4.5 4.4	4.5	4.5	5.1 6.6	5.9	5.9
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
19-May-14	Cloudy	Moderate	10:32	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	26.4 26.4	26.4	7.6 7.6	7.6	17.2 17.2	17.2	85.8 86.2	86.0	6.3 6.3	6.3	6.3	6.3	6.3	6.3	2.4 2.5	2.5	2.5	3.2 2.7	3.0	3.0
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
21-May-14	Cloudy	Moderate	12:15	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
					Middle	0.7	26.6 26.6	26.6	7.6 7.6	7.6	15.7 15.7	15.7	86.3 86.7	86.5	6.4 6.4	6.4	6.4	6.4	6.4	6.4	3.3 3.3	3.3	3.3	5.8 5.7	5.8	5.8
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR3 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)					
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*		
23-May-14	Cloudy	Moderate	13:01	1.8	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.9	<u>26.4</u> 26.4	26.4	7.5 7.5	7.5	17.1 17.1	17.1	86.8 85.3	86.1	6.4 6.2	6.3	6.3	4.8 4.9	4.9	4.9	3.5 3.9	3.7	3.7	3.7
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
26-May-14	Sunny	Moderate	16:54	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.8	<u>28.6</u> 28.6	28.6	7.8 7.8	7.8	14.5 14.5	14.5	119.6 120.9	120.3	8.6 8.6	8.6	8.6	3.0 2.9	3.0	3.0	5.4 4.7	5.1	5.1	5.1
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
28-May-14	Sunny	Moderate	18:31	1.4	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.7	<u>28.5</u> 28.4	28.5	8.7 8.6	8.7	18.7 18.9	18.8	150.3 150.1	150.2	10.5 10.5	10.5	10.5	4.5 4.6	4.6	4.6	5.5 6.2	5.9	5.9	5.9
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
30-May-14	Sunny	Moderate	07:41	1.6	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
					Middle	0.8	<u>27.7</u> 27.7	27.7	8.4 8.4	8.4	17.1 17.1	17.1	109.3 109.9	109.6	7.8 7.9	7.8	7.8	2.0 2.0	2.0	2.0	4.4 3.6	4.0	4.0	4.0
					Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR4(N) - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-May-14	Sunny	Moderate	14:21	3.6	Surface	1.0	24.4 24.5	24.5	8.3 8.3	8.3	26.3 26.3	26.3	90.0 90.3	90.2	6.5 6.5	6.5	6.5	3.6 3.5	3.6	4.3	4.7 5.4	5.1	4.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.6	24.1 24.2	24.1	8.3 8.3	8.3	26.7 26.7	26.7	88.4 88.5	88.5	6.4 6.4	6.4		4.9 4.8	4.9		6.4	4.9 4.8		4.9	3.8 3.5	3.7
5-May-14	Sunny	Moderate	16:18	3.6	Surface	1.0	24.2 24.2	24.2	8.4 8.4	8.4	27.1 26.8	27.0	96.3 97.6	97.0	6.9 7.0	7.0	7.0	5.2 5.0	5.1	5.1	4.5 4.1	4.3	4.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.6	24.2 24.2	24.2	8.4 8.4	8.4	27.2 27.2	27.2	98.7 96.9	97.8	7.1 7.0	7.0		5.2 4.9	5.1		7.0	4.9 4.7		5.1	3.0 4.5	3.8
7-May-14	Cloudy	Moderate	17:50	3.4	Surface	1.0	23.4 23.3	23.4	8.3 8.3	8.3	27.2 27.8	27.5	85.1 97.7	91.4	6.1 7.0	6.6	6.6	4.7 4.7	4.7	4.8	6.1 6.8	6.5	5.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.4	23.4 23.3	23.4	8.4 8.3	8.4	28.8 29.0	28.9	85.8 84.0	84.9	6.2 6.1	6.2		4.9 4.7	4.8		6.2	4.9 4.7		4.8	5.2 4.9	5.1
9-May-14	Rainy	Moderate	14:22	3.7	Surface	1.0	23.4 23.4	23.4	8.4 8.4	8.4	27.9 27.9	27.9	86.8 86.5	86.7	6.3 6.3	6.3	6.3	11.5 11.4	11.5	11.4	5.9 5.1	5.5	7.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	23.5 23.5	23.5	8.3 8.3	8.3	29.6 29.3	29.5	87.2 87.9	87.6	6.3 6.3	6.3		11.2 11.2	11.2		6.3	11.2 11.2		11.2	9.0 8.6	8.8
12-May-14	Sunny	Moderate	11:59	3.4	Surface	1.0	23.6 23.6	23.6	8.1 8.1	8.1	10.4 12.0	11.2	87.5 91.8	89.7	6.9 7.0	7.0	7.0	7.1 7.1	7.1	7.2	5.5 5.1	5.3	5.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.4	23.4 23.5	23.5	8.1 8.0	8.1	18.1 18.3	18.2	87.5 86.4	87.0	6.9 6.7	6.8		7.1 7.2	7.2		6.8	7.1 7.2		7.2	4.0 5.5	4.8
14-May-14	Sunny	Moderate	13:22	3.8	Surface	1.0	25.4 25.4	25.4	7.6 7.6	7.6	18.2 17.9	18.1	80.2 80.5	80.4	5.9 6.0	6.0	6.0	6.3 6.5	6.4	6.4	3.5 2.8	3.2	3.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.8	25.1 25.0	25.1	7.6 7.6	7.6	19.5 19.6	19.5	79.7 81.0	80.4	5.9 6.0	5.9		6.4 6.4	6.4		5.9	6.4 6.4		6.4	3.1 4.0	3.6
16-May-14	Cloudy	Moderate	13:34	3.7	Surface	1.0	26.6 26.7	26.7	7.6 7.6	7.6	17.2 17.1	17.2	84.7 86.8	85.8	6.2 6.3	6.2	6.2	4.6 4.8	4.7	4.8	2.9 3.3	3.1	3.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	26.2 26.1	26.1	7.5 7.5	7.5	18.1 18.2	18.1	83.7 87.9	85.8	6.1 6.4	6.3		4.7 4.8	4.8		6.3	4.7 4.8		4.8	3.1 2.9	3.0
19-May-14	Sunny	Rough	15:41	3.7	Surface	1.0	26.9 26.8	26.9	7.4 7.4	7.4	15.9 15.9	15.9	81.0 79.3	80.2	5.9 5.8	5.9	5.9	5.5 5.3	5.4	5.7	3.9 3.6	3.8	5.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	26.7 26.8	26.8	7.4 7.3	7.4	16.1 16.1	16.1	79.2 81.7	80.5	5.8 6.0	5.9		6.0 5.7	5.9		5.9	6.0 5.7		5.9	6.8 7.5	7.2
21-May-14	Cloudy	Moderate	17:41	3.7	Surface	1.0	26.8 26.8	26.8	7.6 7.6	7.6	12.3 11.8	12.1	82.5 84.8	83.7	6.2 6.4	6.3	6.3	8.4 8.2	8.3	8.4	7.5 7.2	7.4	7.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.7	26.4 26.5	26.4	7.6 7.6	7.6	16.1 15.9	16.0	81.2 83.5	82.4	6.0 6.1	6.1		8.4 8.3	8.4		6.1	8.4 8.3		8.4	6.3 7.0	6.7

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR4(N) - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	09:24	3.5	Surface	1.0	26.6 26.6	26.6	7.7 7.7	7.7	14.0 13.8	13.9	79.4 84.5	82.0	5.9 6.3	6.1	6.1	3.2 3.5	3.4	4.1	3.1 2.8	3.0	3.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.5	26.4 26.4	26.4	7.6 7.5	7.6	18.2 18.3	18.3	79.2 74.6	76.9	5.9 5.4	5.7		5.7	4.5 4.8		4.7	5.7		4.5 4.8	4.7	5.7	3.4 3.7
26-May-14	Sunny	Moderate	12:04	3.7	Surface	1.0	27.7 27.7	27.7	7.6 7.6	7.6	14.6 14.8	14.7	91.8 88.5	90.2	6.7 6.4	6.5	6.5	2.2 2.0	2.1	2.3	2.0 2.7	2.4	3.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	27.8 27.2	27.5	7.6 7.5	7.5	15.6 15.5	15.5	92.7 83.4	88.1	6.7 6.1	6.4		6.4	2.4 2.5		2.5	6.4		2.4 2.5	2.5	6.4	4.8 4.8
28-May-14	Sunny	Moderate	13:10	3.7	Surface	1.0	28.8 28.8	28.8	8.6 8.6	8.6	14.8 14.8	14.8	138.8 136.9	137.9	9.9 9.7	9.8	9.8	4.7 4.7	4.7	4.8	7.4 5.1	6.3	6.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.7	28.7 28.7	28.7	8.5 8.6	8.6	14.9 14.9	14.9	133.7 137.7	135.7	9.5 9.8	9.7		9.7	4.7 4.8		4.8	9.7		4.7 4.8	4.8	9.7	6.0 5.4
30-May-14	Sunny	Moderate	13:07	3.4	Surface	1.0	28.5 28.2	28.4	8.5 8.4	8.5	15.4 16.1	15.8	113.0 118.1	115.6	8.1 8.4	8.2	8.2	2.4 2.5	2.5	2.5	3.2 3.0	3.1	2.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.4	29.2 28.6	28.9	8.6 8.5	8.6	16.3 17.7	17.0	106.6 117.3	112.0	7.5 8.3	7.9		7.9	2.5 2.5		2.5	7.9		2.5 2.5	2.5	7.9	2.6 2.8

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR4(N) - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-May-14	Sunny	Moderate	08:01	3.6	Surface	1.0	23.9 23.9	23.9	8.4 8.4	8.4	26.3 26.3	26.3	86.6 86.1	86.4	6.3 6.3	6.3	6.3	4.4 4.3	4.4	4.7	3.4 3.6	3.5	4.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.6	23.9 23.9	23.9	8.4 8.4	8.4	26.9 26.8	26.9	85.6 85.7	85.7	6.2 6.2	6.2		5.0 4.9	5.0		6.2	5.0 4.9		5.0	5.5 5.6	5.6	
5-May-14	Sunny	Moderate	09:35	3.8	Surface	1.0	24.2 24.2	24.2	8.3 8.4	8.4	24.8 24.8	24.8	91.9 92.1	92.0	6.7 6.7	6.7	6.7	3.0 3.1	3.1	4.2	4.2 4.0	4.1	3.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.8	24.2 24.2	24.2	8.3 8.4	8.3	25.5 25.2	25.4	91.5 91.9	91.7	6.6 6.7	6.7		5.3 5.0	5.2		6.7	5.3 5.0		5.2	3.2 3.2	3.2	
7-May-14	Cloudy	Moderate	11:30	3.7	Surface	1.0	23.4 23.4	23.4	8.4 8.4	8.4	28.3 28.5	28.4	99.1 88.7	93.9	7.2 6.4	6.8	6.8	4.6 4.5	4.6	4.7	4.8 5.0	4.9	6.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.7	23.4 23.3	23.4	8.4 8.4	8.4	29.0 28.5	28.7	89.8 87.9	88.9	6.5 6.4	6.4		4.8 4.5	4.7		6.4	4.8 4.5		4.7	6.9 7.0	7.0	
9-May-14	Rainy	Moderate	10:08	3.8	Surface	1.0	23.3 23.3	23.3	8.4 8.4	8.4	27.9 28.1	28.0	90.8 91.3	91.1	6.6 6.6	6.6	6.6	9.5 9.5	9.5	9.5	14.0 13.9	14.0	13.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.8	23.3 23.4	23.4	8.4 8.3	8.3	28.3 28.6	28.5	91.3 89.5	90.4	6.6 6.5	6.5		9.5 9.5	9.5		6.5	9.5 9.5		9.5	12.7 14.4	13.6	
12-May-14	Sunny	Moderate	17:03	3.4	Surface	1.0	24.7 24.8	24.8	8.1 8.1	8.1	18.6 18.5	18.5	88.4 96.3	92.4	6.6 7.2	6.9	6.9	12.2 12.3	12.3	12.4	5.2 5.0	5.1	4.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.4	24.8 24.7	24.7	8.1 8.1	8.1	18.5 19.2	18.9	87.6 88.9	88.3	6.6 6.6	6.6		12.6 12.4	12.5		6.6	12.6 12.4		12.5	4.2 4.2	4.2	
14-May-14	Sunny	Moderate	18:55	3.7	Surface	1.0	25.0 25.0	25.0	7.6 7.6	7.6	21.8 21.8	21.8	82.4 84.3	83.4	6.0 6.2	6.1	6.1	20.5 20.4	20.5	20.4	5.0 5.7	5.4	5.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.7	25.0 25.0	25.0	7.6 7.5	7.6	21.8 21.8	21.8	83.3 87.1	85.2	6.1 6.4	6.2		20.1 20.5	20.3		6.2	20.1 20.5		20.3	4.7 5.0	4.9	
16-May-14	Cloudy	Moderate	07:20	3.8	Surface	1.0	25.5 25.5	25.5	7.6 7.6	7.6	17.8 17.7	17.8	80.7 79.0	79.9	6.0 5.9	5.9	5.9	7.9 7.7	7.8	7.9	6.7 6.6	6.7	7.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.8	25.5 25.5	25.5	7.6 7.6	7.6	17.8 17.7	17.8	83.6 79.8	81.7	6.2 5.9	6.1		8.0 7.9	8.0		6.1	8.0 7.9		8.0	7.2 8.0	7.6	
19-May-14	Cloudy	Moderate	09:47	3.8	Surface	1.0	26.0 26.0	26.0	7.5 7.5	7.5	16.1 15.6	15.9	72.9 75.6	74.3	5.4 5.6	5.5	5.5	9.4 9.0	9.2	9.1	5.8 6.2	6.0	10.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.8	26.0 25.9	26.0	7.5 7.4	7.5	16.2 16.1	16.2	74.0 74.9	74.5	5.5 5.6	5.5		9.1 8.6	8.9		5.5	9.1 8.6		8.9	14.2 13.8	14.0	
21-May-14	Cloudy	Moderate	11:36	3.9	Surface	1.0	26.4 26.4	26.4	7.6 7.6	7.6	15.8 15.8	15.8	83.1 81.1	82.1	6.1 6.0	6.1	6.1	6.4 6.4	6.4	6.6	7.5 6.4	7.0	7.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.9	26.4 26.3	26.4	7.6 7.5	7.6	15.9 15.7	15.8	82.0 85.4	83.7	6.0 6.3	6.2		6.7 6.6	6.7		6.2	6.7 6.6		6.7	7.8 8.5	8.2	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR4(N) - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	13:48	3.4	Surface	1.0	<u>26.5</u> 26.4	26.4	7.6 7.5	7.6	14.1 14.0	14.1	90.1 92.7	91.4	6.7 6.9	6.8	6.8	8.2 7.7	8.0	7.2	3.9 2.5	3.2	3.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	2.4	26.5 26.3	26.4	7.6 7.4	7.5	14.8 14.1	14.5	91.2 94.6	92.9	6.8 7.1	6.9		6.0 6.5	6.3		6.0 6.5	6.3		3.1 3.2	3.2		
26-May-14	Sunny	Moderate	17:48	3.5	Surface	1.0	28.0 28.0	28.0	7.6 7.6	7.6	12.7 13.1	12.9	97.2 98.7	98.0	7.1 7.2	7.1	7.1	13.1 12.7	12.9	15.4	-	-	3.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.5	27.8 27.9	27.9	7.5 7.6	7.6	15.6 15.0	15.3	96.1 98.4	97.3	6.9 7.1	7.0		18.2 17.6	17.9		3.5 2.7	3.1					
28-May-14	Sunny	Moderate	19:13	3.6	Surface	1.0	28.6 28.7	28.7	8.7 8.7	8.7	16.9 16.8	16.9	139.8 140.7	140.3	9.9 9.9	9.9	9.9	7.6 7.3	7.5	7.7	6.3 6.0	6.2	6.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.6	27.3 27.4	27.3	8.5 8.5	8.5	19.3 19.8	19.6	124.8 123.9	124.4	8.9 8.8	8.8		7.9 7.8	7.9		7.6 7.3	7.5					
30-May-14	Sunny	Moderate	07:00	3.4	Surface	1.0	27.2 27.2	27.2	8.2 8.2	8.2	17.8 17.8	17.8	94.2 79.8	87.0	6.8 5.7	6.3	6.3	2.9 2.7	2.8	3.0	3.1 2.6	2.9	3.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	2.4	27.2 27.1	27.1	8.2 8.2	8.2	18.1 17.8	17.9	79.2 86.2	82.7	5.7 6.2	5.9		3.1 3.1	3.1		3.9 2.9	3.4					

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-May-14	Sunny	Moderate	14:50	4.9	Surface	1.0	24.3 24.3	24.3	8.2 8.2	8.2	26.8 26.9	26.8	91.0 90.1	90.6	6.5 6.5	6.5	6.5	3.3 3.1	3.2	3.2	5.1 4.0	4.6	4.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.9	24.3 24.3	24.3	8.2 8.2	8.2	27.0 27.0	27.0	90.3 93.0	91.7	6.5 6.7	6.6		6.6	3.1 3.3		3.2	3.1 3.3		3.2	4.1 4.4	4.3	4.1 4.3
5-May-14	Sunny	Moderate	16:50	5.0	Surface	1.0	24.3 24.3	24.3	8.3 8.2	8.3	25.8 26.0	25.9	91.9 90.9	91.4	6.6 6.6	6.6	6.6	2.3 2.2	2.3	2.4	4.4 4.6	4.5	4.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.0	24.2 24.2	24.2	8.2 8.2	8.2	27.4 27.7	27.5	92.5 91.0	91.8	6.6 6.5	6.6		6.6	2.4 2.4		2.4	2.4 2.4		2.4	5.2 3.9	4.6	5.2 3.9
7-May-14	Cloudy	Moderate	18:37	4.6	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	29.9 30.0	30.0	91.2 92.9	92.1	6.5 6.6	6.6	6.6	3.7 3.8	3.8	3.8	6.5 5.4	6.0	6.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.6	23.6 23.6	23.6	8.2 8.2	8.2	30.0 30.0	30.0	91.9 95.4	93.7	6.6 6.8	6.7		6.7	3.7 3.7		3.7	3.7 3.7		3.7	5.9 5.8	5.9	5.9 5.8
9-May-14	Rainy	Moderate	09:59	4.7	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	27.9 27.9	27.9	87.5 87.3	87.4	6.3 6.3	6.3	6.3	4.0 4.4	4.2	4.6	4.3 4.4	4.4	5.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.7	23.7 23.7	23.7	8.2 8.2	8.2	30.2 30.1	30.1	87.4 87.0	87.2	6.2 6.2	6.2		6.2	4.9 5.1		5.0	4.9 5.1		5.0	6.6 7.9	7.3	6.6 7.9
12-May-14	Sunny	Moderate	11:44	4.8	Surface	1.0	24.0 24.0	24.0	8.0 8.0	8.0	14.4 14.2	14.3	84.3 84.4	84.4	6.5 6.6	6.5	6.5	3.9 3.8	3.9	3.9	5.4 5.6	5.5	5.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.8	24.0 23.9	23.9	8.0 8.0	8.0	17.3 17.4	17.4	84.4 84.1	84.3	6.4 6.4	6.4		6.4	3.9 3.8		3.9	3.9 3.8		3.9	6.4 4.9	5.7	6.4 4.9
14-May-14	Sunny	Moderate	12:54	4.8	Surface	1.0	25.0 25.1	25.1	8.1 8.0	8.1	17.6 17.6	17.6	84.2 84.1	84.2	6.3 6.3	6.3	6.3	5.5 5.4	5.5	6.1	6.9 5.3	6.1	6.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.8	24.9 25.0	25.0	8.0 8.0	8.0	19.8 18.9	19.4	83.9 83.9	83.9	6.2 6.2	6.2		6.2	6.7 6.5		6.6	6.7 6.5		6.6	7.4 5.8	6.6	7.4 5.8
16-May-14	Cloudy	Moderate	13:36	5.5	Surface	1.0	25.4 25.4	25.4	8.1 8.1	8.1	18.1 18.6	18.3	81.6 81.7	81.7	6.0 6.0	6.0	6.0	6.7 6.9	6.8	7.0	4.5 5.2	4.9	5.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.5	25.4 25.3	25.3	8.1 8.1	8.1	20.0 20.4	20.2	81.5 81.4	81.5	6.0 6.0	6.0		6.0	7.0 7.2		7.1	7.0 7.2		7.1	5.0 5.3	5.2	5.0 5.3
19-May-14	Sunny	Rough	16:40	5.0	Surface	1.0	26.6 26.8	26.7	8.1 8.1	8.1	14.5 14.4	14.5	88.0 84.5	86.3	6.4 6.2	6.3	6.3	4.5 4.4	4.5	4.6	3.7 2.9	3.3	3.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.0	26.1 26.6	26.3	8.1 8.0	8.1	18.1 17.3	17.7	85.3 84.5	84.9	6.3 6.2	6.2		6.2	4.7 4.6		4.7	4.7 4.6		4.7	4.2 4.1	4.2	4.2 4.1
21-May-14	Cloudy	Moderate	18:03	5.5	Surface	1.0	26.6 26.7	26.6	8.1 8.1	8.1	13.1 13.1	13.1	77.5 78.7	78.1	5.8 5.9	5.8	5.8	3.4 3.8	3.6	4.2	6.1 6.7	6.4	6.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.5	25.8 25.9	25.9	8.0 8.0	8.0	19.1 19.1	19.1	77.3 76.3	76.8	5.7 5.6	5.6		5.6	4.9 4.5		4.7	4.9 4.5		4.7	6.6 7.0	6.8	6.6 7.0

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR5 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	09:17	4.8	Surface	1.0	26.2 <u>26.2</u>	26.2	8.0 <u>8.0</u>	8.0	13.9 <u>13.9</u>	13.9	69.9 <u>70.1</u>	70.0	5.2 <u>5.3</u>	5.2	5.2	4.2 <u>4.0</u>	4.1	4.2	5.3 <u>4.5</u>	4.9	4.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.8	26.1 <u>25.9</u>	26.0	7.9 <u>7.9</u>	7.9	18.3 <u>18.4</u>	18.4	70.5 <u>68.9</u>	69.7	5.2 <u>5.1</u>	5.1		5.1	4.3 <u>4.3</u>		4.3	5.1		4.3 <u>4.3</u>	4.3	4.6 <u>4.6</u>	4.6
26-May-14	Sunny	Moderate	11:59	5.0	Surface	1.0	27.4 <u>27.3</u>	27.3	7.9 <u>7.9</u>	7.9	9.6 <u>10.0</u>	9.8	73.8 <u>72.6</u>	73.2	5.5 <u>5.4</u>	5.5	5.5	4.4 <u>4.5</u>	4.5	4.5	4.1 <u>3.9</u>	4.0	4.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.0	27.1 <u>26.7</u>	26.9	7.8 <u>7.8</u>	7.8	13.7 <u>14.0</u>	13.8	73.5 <u>71.3</u>	72.4	5.4 <u>5.3</u>	5.4		5.4	4.4 <u>4.5</u>		4.5	5.4		4.4 <u>4.5</u>	4.5	3.7 <u>4.1</u>	3.9
28-May-14	Sunny	Moderate	12:39	4.8	Surface	1.0	27.5 <u>27.4</u>	27.5	8.1 <u>8.1</u>	8.1	15.4 <u>15.4</u>	15.4	85.2 <u>85.6</u>	85.4	6.2 <u>6.2</u>	6.2	6.2	2.0 <u>2.1</u>	2.1	2.2	3.0 <u>3.5</u>	3.3	3.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.8	27.2 <u>27.5</u>	27.4	8.1 <u>8.1</u>	8.1	17.6 <u>17.6</u>	17.6	84.6 <u>84.9</u>	84.8	6.1 <u>6.1</u>	6.1		6.1	2.2 <u>2.2</u>		2.2	6.1		2.2 <u>2.2</u>	2.2	3.3 <u>2.9</u>	3.1
30-May-14	Sunny	Moderate	13:47	4.7	Surface	1.0	27.5 <u>27.6</u>	27.6	8.1 <u>8.1</u>	8.1	14.6 <u>14.6</u>	14.6	85.3 <u>87.1</u>	86.2	6.2 <u>6.3</u>	6.3	6.3	2.2 <u>2.3</u>	2.3	2.4	2.6 <u>2.6</u>	2.6	2.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.7	27.2 <u>27.1</u>	27.2	8.1 <u>8.1</u>	8.1	17.7 <u>17.9</u>	17.8	86.5 <u>83.7</u>	85.1	6.2 <u>6.0</u>	6.1		6.1	2.5 <u>2.5</u>		2.5	6.1		2.5 <u>2.5</u>	2.5	2.6 <u>2.9</u>	2.8

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-May-14	Sunny	Moderate	08:10	5.2	Surface	1.0	23.9 23.9	23.9	8.2 8.2	8.2	27.4 27.2	27.3	84.9 85.0	85.0	6.1 6.1	6.1	6.1	6.7 6.9	6.8	6.9	4.7 6.1	5.4	6.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.2	23.8 23.9	23.9	8.2 8.2	8.2	28.0 27.7	27.9	84.7 84.9	84.8	6.1 6.1	6.1		6.1	6.9 6.8		6.9	6.1		6.9 6.8	6.9	7.9 6.2	7.1
5-May-14	Sunny	Moderate	09:47	5.2	Surface	1.0	24.3 24.3	24.3	8.2 8.2	8.2	22.2 22.1	22.1	87.8 87.9	87.9	6.5 6.5	6.5	6.5	2.7 2.7	2.7	2.8	4.4 2.4	3.4	3.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.2	24.1 24.1	24.1	8.1 8.1	8.1	28.2 28.5	28.3	87.4 87.7	87.6	6.3 6.3	6.3		6.3	2.8 2.7		2.8	6.3		2.8 2.7	2.8	3.3 2.7	3.0
7-May-14	Cloudy	Moderate	11:36	5.3	Surface	1.0	23.6 23.7	23.7	8.2 8.2	8.2	30.0 30.0	30.0	87.8 87.7	87.8	6.3 6.3	6.3	6.3	4.6 4.7	4.7	4.7	6.1 7.5	6.8	7.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.3	23.7 23.7	23.7	8.2 8.2	8.2	30.3 30.5	30.4	87.8 87.8	87.8	6.3 6.2	6.2		6.2	4.7 4.7		4.7	6.2		4.7 4.7	4.7	9.3 7.6	8.5
9-May-14	Rainy	Moderate	14:36	4.9	Surface	1.0	23.6 23.6	23.6	8.1 8.0	8.0	28.6 28.4	28.5	88.5 89.8	89.2	6.4 6.5	6.4	6.4	5.6 5.9	5.8	6.2	4.3 3.7	4.0	5.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.9	23.7 23.7	23.7	8.0 8.0	8.0	30.4 30.5	30.4	92.1 89.3	90.7	6.6 6.4	6.5		6.5	6.7 6.3		6.5	6.5		6.7 6.3	6.5	6.6 6.4	6.5
12-May-14	Sunny	Moderate	17:36	4.8	Surface	1.0	24.6 24.5	24.5	7.8 7.9	7.9	14.3 14.8	14.6	85.2 84.4	84.8	6.5 6.5	6.5	6.5	5.4 5.5	5.5	5.5	5.4 3.4	4.4	4.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.8	24.3 24.4	24.3	7.7 7.8	7.7	17.8 17.6	17.7	85.3 84.4	84.9	6.5 6.4	6.4		6.4	5.5 5.3		5.4	6.4		5.5 5.3	5.4	4.3 3.7	4.0
14-May-14	Sunny	Moderate	19:11	4.7	Surface	1.0	25.8 25.8	25.8	8.0 8.0	8.0	13.8 13.9	13.9	87.4 86.4	86.9	6.6 6.5	6.5	6.5	7.0 7.3	7.2	7.6	5.3 5.8	5.6	5.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.7	25.6 25.7	25.6	8.0 7.9	8.0	17.3 17.4	17.4	89.0 86.2	87.6	6.6 6.4	6.5		6.5	8.0 8.0		8.0	6.5		8.0 8.0	8.0	4.5 4.3	4.4
16-May-14	Cloudy	Moderate	08:19	5.5	Surface	1.0	25.3 25.3	25.3	8.0 8.0	8.0	19.4 19.5	19.4	79.5 79.4	79.5	5.9 5.8	5.8	5.8	10.6 10.9	10.8	10.9	8.1 7.5	7.8	7.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.5	25.3 25.3	25.3	8.0 8.0	8.0	19.4 19.5	19.5	79.5 79.4	79.5	5.9 5.8	5.8		5.8	10.7 11.0		10.9	5.8		10.7 11.0	10.9	8.1 7.7	7.9
19-May-14	Cloudy	Moderate	09:47	5.0	Surface	1.0	26.0 26.0	26.0	7.9 7.9	7.9	14.7 14.6	14.7	76.3 76.4	76.4	5.7 5.7	5.7	5.7	3.8 3.9	3.9	3.9	6.0 6.5	6.3	7.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.0	26.0 26.0	26.0	7.9 7.9	7.9	15.4 14.8	15.1	76.3 76.2	76.3	5.7 5.7	5.7		5.7	4.0 3.8		3.9	5.7		4.0 3.8	3.9	7.2 8.7	8.0
21-May-14	Cloudy	Moderate	11:53	5.4	Surface	1.0	26.1 26.1	26.1	8.0 8.0	8.0	14.5 14.4	14.5	78.3 79.1	78.7	5.9 5.9	5.9	5.9	5.3 5.0	5.2	5.3	3.3 4.5	3.9	4.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.4	26.0 26.0	26.0	8.0 8.0	8.0	20.0 18.7	19.3	78.3 79.5	78.9	5.7 5.8	5.7		5.7	5.5 5.2		5.4	5.7		5.5 5.2	5.4	4.3 4.6	4.5

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR5 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	14:22	5.3	Surface	1.0	<u>26.4</u> <u>26.4</u>	26.4	7.9 7.9	7.9	11.8 11.7	11.8	79.1 80.2	79.7	6.0 6.0	6.0	6.0	3.9 3.7	3.8	4.0	5.0 4.7	4.9	5.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.3	<u>26.3</u> <u>26.2</u>	26.2	7.8 7.8	7.8	15.7 15.8	15.8	80.0 76.9	78.5	5.9 5.7	5.8		5.8	4.1 4.2		4.2	4.1 4.2		4.2	4.8 5.2	5.0	
26-May-14	Sunny	Moderate	17:38	5.0	Surface	1.0	<u>27.7</u> <u>27.7</u>	27.7	8.0 8.0	8.0	10.3 10.7	10.5	86.5 88.0	87.3	6.4 6.5	6.5	6.5	4.5 4.3	4.4	4.4	4.0 3.9	4.0	4.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.0	<u>27.7</u> <u>27.7</u>	27.7	7.9 8.0	8.0	13.0 12.9	13.0	86.2 91.8	89.0	6.3 6.7	6.5		6.5	4.3 4.2		4.3	4.3 4.2		4.3	3.3 5.0	4.2	
28-May-14	Sunny	Moderate	18:52	4.6	Surface	1.0	<u>27.9</u> <u>27.9</u>	27.9	8.1 8.1	8.1	9.4 9.2	9.3	92.6 95.0	93.8	6.8 7.0	6.9	6.9	4.7 4.6	4.7	4.8	4.1 4.7	4.4	4.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.6	<u>27.8</u> <u>27.8</u>	27.8	8.0 8.0	8.0	11.9 12.0	12.0	93.1 91.9	92.5	6.9 6.8	6.9		6.9	4.8 4.7		4.8	4.8 4.7		4.8	5.4 4.4	4.9	
30-May-14	Sunny	Moderate	07:17	4.8	Surface	1.0	<u>27.0</u> <u>27.1</u>	27.1	8.1 8.1	8.1	18.7 18.6	18.7	76.5 79.7	78.1	5.5 5.7	5.6	5.6	5.2 5.5	5.4	5.4	4.3 3.9	4.1	4.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.8	<u>26.6</u> <u>27.0</u>	26.8	8.1 8.1	8.1	21.4 20.4	20.9	74.1 79.1	76.6	5.3 5.6	5.4		5.4	5.2 5.3		5.3	5.2 5.3		5.3	4.8 4.2	4.5	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-May-14	Sunny	Moderate	13:51	4.2	Surface	1.0	24.5 24.5	24.5	8.2 8.2	8.2	26.8 26.8	26.8	91.1 91.3	91.2	6.5 6.5	6.5	6.5	3.1 3.1	3.1	3.2	4.4 4.7	4.6	4.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.2	24.4 24.5	24.4	8.2 8.2	8.2	27.4 27.1	27.2	91.2 90.9	91.1	6.5 6.5	6.5		6.5	3.3 3.1		3.2	4.2 4.9		4.6		
5-May-14	Sunny	Moderate	15:53	4.2	Surface	1.0	24.3 24.4	24.4	8.3 8.3	8.3	24.7 24.9	24.8	92.3 92.1	92.2	6.7 6.7	6.7	6.7	2.2 2.2	2.2	2.2	3.4 4.1	3.8	4.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.2	24.3 24.3	24.3	8.2 8.3	8.3	26.5 26.7	26.6	91.8 90.1	91.0	6.6 6.5	6.5		6.5	2.3 2.1		2.2	4.0 5.4		4.7		
7-May-14	Cloudy	Moderate	17:36	4.1	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	28.2 28.1	28.1	91.8 91.8	91.8	6.6 6.6	6.6	6.6	1.8 1.8	1.8	2.0	5.8 6.1	6.0	6.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.1	23.6 23.6	23.6	8.2 8.2	8.2	29.5 29.5	29.5	91.8 91.4	91.6	6.6 6.6	6.6		6.6	2.2 2.2		2.2	6.0 6.3		6.2		
9-May-14	Rainy	Moderate	10:58	3.7	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	28.1 27.9	28.0	88.0 88.0	88.0	6.4 6.4	6.4	6.4	10.8 10.8	10.8	12.3	5.9 6.3	6.1	7.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.7	23.7 23.7	23.7	8.2 8.2	8.2	30.0 29.8	29.9	87.8 87.6	87.7	6.3 6.3	6.3		6.3	14.0 13.5		13.8	8.8 6.8		7.8		
12-May-14	Sunny	Moderate	12:51	4.1	Surface	1.0	24.3 24.4	24.3	8.0 8.0	8.0	13.0 12.7	12.9	82.7 83.0	82.9	6.4 6.5	6.4	6.4	3.6 3.6	3.6	3.7	4.4 5.1	4.8	5.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.1	24.0 23.9	24.0	7.9 7.9	7.9	15.5 15.7	15.6	82.3 82.1	82.2	6.3 6.3	6.3		6.3	3.8 3.6		3.7	5.2 6.4		5.8		
14-May-14	Sunny	Moderate	13:48	3.9	Surface	1.0	25.3 25.3	25.3	8.0 8.0	8.0	17.1 17.2	17.2	84.5 84.0	84.3	6.3 6.3	6.3	6.3	3.8 3.7	3.8	3.9	6.9 6.6	6.8	6.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	2.9	25.0 25.0	25.0	8.0 8.0	8.0	18.2 17.6	17.9	83.6 82.4	83.0	6.2 6.2	6.2		6.2	4.0 3.8		3.9	6.6 6.3		6.5		
16-May-14	Cloudy	Moderate	13:01	5.5	Surface	1.0	25.6 25.5	25.6	8.0 8.0	8.0	17.5 17.6	17.5	82.8 82.7	82.8	6.1 6.1	6.1	6.1	6.2 6.5	6.4	6.5	5.1 4.8	5.0	5.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.5	25.3 25.4	25.3	8.0 8.0	8.0	20.4 20.3	20.4	82.4 82.3	82.4	6.0 6.0	6.0		6.0	6.6 6.4		6.5	4.5 6.0		5.3		
19-May-14	Sunny	Rough	15:54	4.9	Surface	1.0	26.7 26.4	26.6	8.1 8.1	8.1	14.3 14.6	14.5	84.9 84.1	84.5	6.3 6.2	6.3	6.3	4.2 4.3	4.3	4.4	5.0 4.9	5.0	6.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.9	26.3 26.7	26.5	8.1 8.1	8.1	17.3 17.3	17.3	84.1 84.3	84.2	6.2 6.1	6.1		6.1	4.4 4.3		4.4	6.9 6.9		6.9		
21-May-14	Cloudy	Moderate	17:05	4.4	Surface	1.0	26.5 26.5	26.5	8.1 8.1	8.1	12.9 12.9	12.9	77.8 77.9	77.9	5.8 5.8	5.8	5.8	3.2 3.2	3.2	3.3	6.1 5.6	5.9	5.7			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	3.4	26.0 26.1	26.1	8.0 8.0	8.0	16.8 18.5	17.7	76.2 76.8	76.5	5.6 5.6	5.6		5.6	3.5 3.3		3.4	6.4 4.3		5.4		

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR6 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	10:18	4.2	Surface	1.0	<u>26.4</u> 26.4	26.4	8.0 8.0	8.0	11.0 11.0	11.0	74.8 74.3	74.6	5.7 5.6	5.7	5.7	3.8 3.9	3.9	3.9	4.8 4.4	4.6	4.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.2	26.1 26.0	26.1	7.9 8.0	7.9	16.4 14.9	15.7	72.8 69.4	71.1	5.4 5.2	5.3		5.3	3.8 3.7		3.8	5.3		3.8	3.8	4.9 5.2	5.1
26-May-14	Sunny	Moderate	12:58	4.0	Surface	1.0	27.2 27.1	27.2	7.9 7.9	7.9	9.7 9.9	9.8	70.0 69.9	70.0	5.3 5.3	5.3	5.3	4.5 4.6	4.6	4.6	3.7 3.4	3.6	4.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.0	26.8 26.8	26.8	7.8 7.8	7.8	13.3 13.3	13.3	69.7 69.0	69.4	5.2 5.1	5.1		5.1	4.6 4.6		4.6	5.1		4.6	4.6	4.2 4.5	4.4
28-May-14	Sunny	Moderate	13:16	5.1	Surface	1.0	27.4 26.9	27.2	8.1 8.1	8.1	17.9 15.6	16.8	80.3 77.3	78.8	5.7 5.6	5.7	5.7	3.3 3.0	3.2	3.2	4.1 2.5	3.3	4.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.1	27.2 26.6	26.9	8.1 8.1	8.1	20.3 21.3	20.8	78.4 76.3	77.4	5.6 5.5	5.5		5.5	3.1 3.2		3.2	5.5		3.1	3.2	5.5	5.5
30-May-14	Sunny	Moderate	12:52	4.1	Surface	1.0	27.3 27.7	27.5	8.2 8.2	8.2	15.2 14.4	14.8	84.5 86.1	85.3	6.2 6.3	6.2	6.2	1.8 1.8	1.8	1.8	2.2 4.1	3.2	3.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	27.0 27.2	27.1	8.1 8.1	8.1	19.0 19.0	19.0	85.0 85.0	85.0	6.1 6.1	6.1		6.1	1.8 1.7		1.8	6.1		1.8	1.8	4.4 2.5	3.5

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-May-14	Sunny	Moderate	09:07	4.1	Surface	1.0	24.0 24.0	24.0	8.2 8.1	8.2	25.4 25.4	25.4	85.7 85.5	85.6	6.2 6.2	6.2	6.2	3.3 3.4	3.4	3.5	3.8 3.8	3.8	4.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.1	24.0 23.9	23.9	8.1 8.2	8.2	26.6 26.8	26.7	85.5 85.3	85.4	6.2 6.2	6.2		6.2	3.4 3.5		3.5	6.2		3.4 3.5	3.5	6.2
5-May-14	Sunny	Moderate	10:47	4.4	Surface	1.0	24.3 24.3	24.3	8.2 8.2	8.2	22.2 22.2	22.2	87.6 87.7	87.7	6.5 6.5	6.5	6.5	5.4 5.3	5.4	5.7	2.9 2.1	2.5	2.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.4	24.2 24.1	24.1	8.1 8.2	8.2	27.4 28.2	27.8	87.3 87.1	87.2	6.3 6.2	6.2		6.2	6.0 5.8		5.9	6.2		6.0 5.8	5.9	6.2
7-May-14	Cloudy	Moderate	12:36	4.2	Surface	1.0	23.5 23.5	23.5	8.2 8.2	8.2	29.7 29.7	29.7	90.3 90.1	90.2	6.5 6.5	6.5	6.5	2.0 2.0	2.0	2.1	5.2 5.2	5.2	5.4			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.2	23.5 23.5	23.5	8.2 8.2	8.2	29.8 29.8	29.8	90.2 90.0	90.1	6.5 6.4	6.5		6.5	2.1 2.1		2.1	6.5		2.1 2.1	2.1	6.5
9-May-14	Rainy	Moderate	13:41	3.9	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	28.2 28.1	28.1	87.6 87.3	87.5	6.3 6.3	6.3	6.3	3.5 3.6	3.6	4.2	5.9 5.3	5.6	6.3			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	2.9	23.7 23.7	23.7	8.2 8.2	8.2	29.5 29.8	29.7	87.2 85.8	86.5	6.2 6.1	6.2		6.2	4.8 4.7		4.8	6.2		4.8 4.7	4.8	6.2
12-May-14	Sunny	Moderate	16:36	4.2	Surface	1.0	24.5 24.7	24.6	8.0 7.9	8.0	14.2 13.8	14.0	82.7 83.0	82.9	6.4 6.4	6.4	6.4	6.4 6.4	6.4	6.6	3.9 3.1	3.5	3.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.2	24.1 24.0	24.1	7.9 8.0	7.9	17.9 17.3	17.6	82.2 81.7	82.0	6.2 6.2	6.2		6.2	6.7 6.8		6.8	6.2		6.7 6.8	6.8	6.2
14-May-14	Sunny	Moderate	18:14	4.1	Surface	1.0	25.6 25.7	25.6	8.0 8.0	8.0	13.9 13.3	13.6	80.8 80.7	80.8	6.1 6.1	6.1	6.1	6.2 6.8	6.5	6.9	5.0 6.3	5.7	5.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.1	25.4 25.4	25.4	8.0 8.0	8.0	16.7 15.4	16.1	81.0 81.1	81.1	6.0 6.1	6.1		6.1	7.6 6.9		7.3	6.1		7.6 6.9	7.3	6.1
16-May-14	Cloudy	Moderate	08:58	5.5	Surface	1.0	25.2 25.2	25.2	8.1 8.1	8.1	20.3 20.2	20.3	79.1 79.1	79.1	5.8 5.8	5.8	5.8	8.6 8.2	8.4	9.0	8.0 8.0	8.0	7.8			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.5	25.1 25.2	25.1	8.0 8.0	8.0	21.0 20.7	20.8	79.2 79.0	79.1	5.8 5.8	5.8		5.8	9.6 9.4		9.5	5.8		9.6 9.4	9.5	5.8
19-May-14	Cloudy	Moderate	10:23	5.2	Surface	1.0	25.9 25.9	25.9	8.0 8.0	8.0	16.1 16.1	16.1	75.2 74.9	75.1	5.6 5.6	5.6	5.6	4.0 4.0	4.0	4.1	9.8 10.8	10.3	10.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.2	25.7 25.9	25.8	8.0 8.0	8.0	17.8 17.3	17.6	75.0 75.2	75.1	5.5 5.6	5.5		5.5	4.2 4.2		4.2	5.5		4.2 4.2	4.2	5.5
21-May-14	Cloudy	Moderate	12:49	4.3	Surface	1.0	26.2 26.2	26.2	8.0 8.0	8.0	14.0 14.1	14.0	72.0 72.0	72.0	5.4 5.4	5.4	5.4	3.2 3.3	3.3	3.9	4.7 3.3	4.0	4.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	3.3	26.1 26.0	26.0	8.0 8.1	8.0	16.0 16.2	16.1	72.2 72.3	72.3	5.4 5.4	5.4		5.4	4.5 4.3		4.4	5.4		4.5 4.3	4.4	5.4

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR6 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)						
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*			
23-May-14	Cloudy	Moderate	13:21	4.1	Surface	1.0	<u>26.4</u> 26.4	26.4	7.9 7.9	7.9	13.1 12.7	12.9	75.8 76.1	76.0	5.7 5.7	5.7	5.7	4.5 4.4	4.5	4.6	4.0 4.1	4.1	4.5		
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-
					Bottom	3.1	<u>26.2</u> <u>25.9</u>	26.0	7.8 7.9	7.9	17.0 17.3	17.2	75.8 72.2	74.0	5.6 5.3	5.4	5.4	4.6 4.5	4.6		4.6	4.6		4.6	4.9 4.8
26-May-14	Sunny	Moderate	16:40	4.2	Surface	1.0	<u>27.8</u> <u>27.8</u>	27.8	7.9 7.9	7.9	8.9 8.9	8.9	81.5 80.8	81.2	6.1 6.0	6.1	6.1	8.1 8.0	8.1	8.1	6.0 7.2	6.6	7.1		
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-
					Bottom	3.2	<u>27.7</u> <u>27.8</u>	27.7	7.9 7.9	7.9	9.1 9.0	9.1	80.3 81.6	81.0	6.0 6.1	6.1	6.1	8.0 7.9	8.0		8.0	8.0		7.8 7.3	7.6
28-May-14	Sunny	Moderate	18:15	4.8	Surface	1.0	<u>27.9</u> <u>27.6</u>	27.8	8.1 8.1	8.1	10.9 10.6	10.7	89.2 88.8	89.0	6.6 6.5	6.5	6.5	5.0 4.9	5.0	5.0	5.1 5.7	5.4	5.5		
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-
					Bottom	3.8	<u>27.4</u> <u>27.6</u>	27.5	8.1 8.1	8.1	14.2 15.1	14.7	87.1 87.6	87.4	6.4 6.4	6.4	6.4	5.0 5.0	5.0		5.0	5.0		4.9 6.2	5.6
30-May-14	Sunny	Moderate	08:17	4.1	Surface	1.0	<u>27.4</u> <u>27.3</u>	27.4	8.2 8.2	8.2	15.6 14.5	15.0	85.9 85.2	85.6	6.2 6.2	6.2	6.2	1.7 1.7	1.7	1.8	3.3 2.5	2.9	2.8		
					Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-
					Bottom	3.1	<u>27.0</u> <u>27.1</u>	27.1	8.1 8.1	8.1	17.9 19.0	18.5	82.4 84.1	83.3	5.9 6.0	6.0	6.0	1.8 1.9	1.9		6.0	1.8 1.9		1.9	2.4 3.0

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR7 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-May-14	Sunny	Moderate	15:19	4.3	Surface	1.0	24.3 24.2	24.3	8.2 8.2	8.2	27.0 27.2	27.1	88.1 88.1	88.1	6.3 6.3	6.3	6.3	4.5 4.3	4.4	4.4	6.7 5.7	6.2	5.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.3	24.2 24.0	24.1	8.2 8.2	8.2	27.2 27.6	27.4	88.0 88.3	88.2	6.3 6.4	6.3		6.3	4.2 4.5		4.4	4.2		4.5	5.6 5.2	5.4	
5-May-14	Sunny	Moderate	17:18	4.1	Surface	1.0	24.2 24.2	24.2	8.2 8.2	8.2	25.8 25.7	25.8	91.1 91.6	91.4	6.6 6.6	6.6	6.6	2.2 2.3	2.3	2.4	2.8 2.0	2.4	3.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.1	24.2 24.2	24.2	8.2 8.2	8.2	27.1 27.3	27.2	91.6 90.8	91.2	6.6 6.5	6.5		6.5	2.5 2.5		2.5	2.5		2.5	3.5 4.8	4.2	
7-May-14	Cloudy	Moderate	19:07	4.1	Surface	1.0	23.6 23.6	23.6	8.2 8.2	8.2	30.1 30.2	30.2	87.6 86.7	87.2	6.3 6.2	6.2	6.2	3.2 3.1	3.2	3.6	8.1 7.1	7.6	7.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.1	23.7 23.7	23.7	8.2 8.2	8.2	30.4 30.5	30.4	87.4 85.2	86.3	6.2 6.1	6.1		6.1	3.8 3.9		3.9	3.9		3.9	7.0 6.6	6.8	
9-May-14	Rainy	Moderate	09:29	3.8	Surface	1.0	23.6 23.6	23.6	8.0 8.0	8.0	28.6 28.7	28.7	89.5 88.5	89.0	6.4 6.4	6.4	6.4	4.5 4.4	4.5	4.5	6.8 6.9	6.9	7.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	2.8	23.6 23.6	23.6	8.0 8.0	8.0	29.2 29.1	29.2	91.3 88.7	90.0	6.6 6.4	6.5		6.5	4.5 4.4		4.5	4.5		4.5	6.5 7.7	7.1	
12-May-14	Sunny	Moderate	11:13	4.1	Surface	1.0	24.0 23.9	24.0	7.7 7.8	7.8	15.2 15.4	15.3	86.5 85.1	85.8	6.7 6.6	6.6	6.6	4.3 4.5	4.4	4.5	3.8 3.0	3.4	4.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	3.1	23.8 23.8	23.8	7.4 7.8	7.6	17.8 17.5	17.7	85.8 85.4	85.6	6.6 6.5	6.5		6.5	4.5 4.7		4.6	4.6		4.6	4.5 5.8	5.2	
14-May-14	Sunny	Moderate	12:23	4.0	Surface	1.0	25.2 25.1	25.2	8.1 8.1	8.1	17.7 18.0	17.9	87.7 87.8	87.8	6.5 6.5	6.5	6.5	6.0 6.2	6.1	5.9	6.1 5.6	5.9	5.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	3.0	25.1 24.8	24.9	8.1 8.1	8.1	18.3 21.1	19.7	87.3 88.2	87.8	6.5 6.5	6.5		6.5	5.6 5.5		5.6	5.6		5.6	5.1 5.0	5.1	
16-May-14	Cloudy	Moderate	14:04	5.6	Surface	1.0	25.6 25.6	25.6	8.0 8.0	8.0	17.3 17.3	17.3	82.9 82.8	82.9	6.1 6.1	6.1	6.1	5.0 5.1	5.1	5.3	4.9 4.6	4.8	4.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	4.6	25.4 25.4	25.4	8.0 8.0	8.0	18.8 19.0	18.9	82.6 82.3	82.5	6.1 6.1	6.1		6.1	5.4 5.6		5.5	5.5		5.5	5.0 5.0	5.0	
19-May-14	Sunny	Rough	17:00	4.4	Surface	1.0	26.3 26.4	26.4	8.1 8.1	8.1	15.6 15.8	15.7	82.7 83.5	83.1	6.1 6.2	6.1	6.1	4.6 4.4	4.5	4.6	6.3 8.0	7.2	7.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	3.4	25.8 26.4	26.1	8.1 8.1	8.1	19.6 18.8	19.2	82.5 83.1	82.8	6.0 6.0	6.0		6.0	4.6 4.5		4.6	4.6		4.6	6.7 7.8	7.3	
21-May-14	Cloudy	Moderate	18:32	4.4	Surface	1.0	26.6 26.6	26.6	8.0 8.0	8.0	13.2 13.4	13.3	78.4 77.5	78.0	5.8 5.8	5.8	5.8	2.4 2.3	2.4	2.4	3.5 2.2	2.9	2.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	3.4	26.1 26.2	26.1	8.0 8.0	8.0	16.4 16.4	16.4	74.3 77.5	75.9	5.5 5.7	5.6		5.6	2.2 2.4		2.3	2.3		2.3	2.6 2.8	2.7	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR7 - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	08:48	4.1	Surface	1.0	26.3 26.3	26.3	8.1 8.0	8.1	13.4 13.9	13.7	80.7 79.4	80.1	6.0 5.9	6.0	6.0	2.2 2.3	2.3	2.3	4.4 2.7	3.6	3.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	26.3 26.2	26.2	8.0 8.0	8.0	16.4 16.9	16.7	82.2 79.7	81.0	6.1 5.9	6.0		6.0	2.2 2.2		2.2	6.0		2.2 2.2	2.2	3.6 2.9	3.3
26-May-14	Sunny	Moderate	11:30	4.0	Surface	1.0	27.5 27.4	27.5	8.0 8.0	8.0	9.6 9.7	9.7	78.3 76.4	77.4	5.9 5.7	5.8	5.8	4.5 4.5	4.5	4.5	4.3 4.6	4.5	4.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.0	26.7 27.0	26.8	7.9 7.9	7.9	15.5 14.4	15.0	80.4 76.8	78.6	5.9 5.7	5.8		5.8	4.4 4.5		4.5	5.8		4.4 4.5	4.5	4.5 4.9	4.7
28-May-14	Sunny	Moderate	12:13	5.1	Surface	1.0	27.6 27.5	27.5	8.1 8.1	8.1	15.0 14.9	15.0	90.1 87.6	88.9	6.5 6.4	6.5	6.5	1.7 1.5	1.6	1.7	2.3 2.1	2.2	2.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.1	27.2 27.3	27.3	8.1 8.1	8.1	18.3 17.5	17.9	90.5 88.2	89.4	6.5 6.3	6.4		6.4	1.7 1.6		1.7	6.4		1.7 1.6	1.7	2.2 2.5	2.4
30-May-14	Sunny	Moderate	14:16	4.1	Surface	1.0	27.9 28.0	27.9	8.2 8.2	8.2	14.8 14.7	14.7	92.2 94.0	93.1	6.7 6.8	6.7	6.7	1.8 1.8	1.8	1.8	4.5 5.6	5.1	5.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.1	27.7 27.6	27.6	8.1 8.1	8.1	15.8 16.1	16.0	92.2 91.2	91.7	6.6 6.6	6.6		6.6	1.8 1.7		1.8	6.6		1.8 1.7	1.8	4.8 5.7	5.3

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR7 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-May-14	Sunny	Moderate	07:41	4.2	Surface	1.0	23.9 23.9	23.9	8.1 8.1	8.1	27.2 27.0	27.1	86.8 88.1	87.5	6.3 6.4	6.3	6.3	4.1 4.1	4.1	4.7	4.4 3.9	4.2	4.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.2	23.9 23.9	23.9	8.1 8.1	8.1	27.6 27.7	27.7	89.6 87.3	88.5	6.5 6.3	6.4		6.4	5.2 5.2		5.2	3.4 4.5		4.0			
5-May-14	Sunny	Moderate	09:19	4.2	Surface	1.0	24.2 24.2	24.2	8.2 8.2	8.2	26.0 26.0	26.0	91.1 90.6	90.9	6.6 6.6	6.6	6.6	1.9 1.9	1.9	2.0	2.8 3.9	3.4	4.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.2	24.1 24.1	24.1	8.2 8.2	8.2	27.5 27.5	27.5	91.8 90.7	91.3	6.6 6.5	6.6		6.6	2.0 2.0		2.0	5.0 5.2		5.1			
7-May-14	Cloudy	Moderate	11:07	4.2	Surface	1.0	23.7 23.7	23.7	8.2 8.2	8.2	30.2 30.2	30.2	88.7 90.0	89.4	6.3 6.4	6.4	6.4	3.5 3.5	3.5	3.7	5.8 5.3	5.6	5.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.2	23.7 23.7	23.7	8.2 8.2	8.2	30.3 30.4	30.3	89.2 92.0	90.6	6.3 6.5	6.4		6.4	3.7 3.8		3.8	4.8 5.9		5.4			
9-May-14	Rainy	Moderate	15:05	4.1	Surface	1.0	23.4 23.4	23.4	8.2 8.1	8.1	29.3 29.3	29.3	89.4 92.3	90.9	6.4 6.6	6.5	6.5	5.6 6.0	5.8	5.9	7.1 8.2	7.7	8.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	3.1	23.4 23.5	23.5	8.0 8.2	8.1	29.3 29.6	29.4	93.9 89.2	91.6	6.8 6.4	6.6		6.6	6.0 6.0		6.0	8.4 8.7		8.6			
12-May-14	Sunny	Moderate	18:07	4.2	Surface	1.0	24.8 24.8	24.8	8.0 8.0	8.0	16.3 16.7	16.5	85.6 85.9	85.8	6.5 6.5	6.5	6.5	5.5 5.4	5.5	5.6	3.8 4.9	4.4	5.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	3.2	24.5 24.4	24.5	8.0 8.0	8.0	18.5 18.6	18.5	85.2 85.0	85.1	6.4 6.4	6.4		6.4	5.7 5.6		5.7	6.0 6.2		6.1			
14-May-14	Sunny	Moderate	19:41	4.3	Surface	1.0	25.7 25.6	25.7	8.0 8.0	8.0	16.0 16.1	16.0	84.8 84.7	84.8	6.3 6.3	6.3	6.3	5.7 5.8	5.8	5.9	7.1 6.1	6.6	6.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	3.3	25.6 25.5	25.5	8.0 8.0	8.0	17.4 17.4	17.4	84.6 85.4	85.0	6.3 6.3	6.3		6.3	6.0 6.0		6.0	6.5 6.2		6.4			
16-May-14	Cloudy	Moderate	07:47	5.5	Surface	1.0	25.2 25.2	25.2	8.0 7.9	7.9	19.8 19.7	19.8	81.5 81.8	81.9	6.0 6.1	6.0	6.0	4.7 4.6	4.7	4.9	6.4 7.1	6.8	6.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	4.5	25.2 25.2	25.2	7.9 7.9	7.9	19.9 19.8	19.9	83.0 81.8	82.4	6.1 6.0	6.1		6.1	5.0 4.9		5.0	7.0 6.3		6.7			
19-May-14	Cloudy	Moderate	09:24	4.4	Surface	1.0	25.8 25.8	25.8	8.0 8.0	8.0	16.3 16.4	16.4	77.5 75.5	76.5	5.8 5.6	5.7	5.7	3.6 3.7	3.7	3.8	5.2 4.9	5.1	6.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	3.4	25.8 25.7	25.7	8.0 8.1	8.0	16.5 16.9	16.7	75.0 75.8	75.4	5.6 5.6	5.6		5.6	3.9 3.9		3.9	6.4 7.4		6.9			
21-May-14	Cloudy	Moderate	11:25	4.4	Surface	1.0	26.0 26.0	26.0	8.0 8.0	8.0	13.9 14.7	14.3	74.6 74.6	74.6	5.6 5.6	5.6	5.6	6.8 6.3	6.6	8.2	4.3 4.7	4.5	5.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	3.4	25.8 25.8	25.8	8.1 8.0	8.0	17.0 18.0	17.5	74.0 73.9	74.0	5.5 5.4	5.5		5.5	9.4 10.2		9.8	4.7 6.1		5.4			

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR7 - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	14:51	4.2	Surface	1.0	<u>26.4</u> 26.4	26.4	8.0 8.0	8.0	14.9 14.9	14.9	86.8 85.7	86.3	6.4 6.4	6.4	6.4	2.4 2.4	2.4	2.4	4.1 3.2	3.7	3.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	3.2	<u>26.4</u> 26.4	26.4	8.0 8.0	8.0	16.3 15.4	15.8	85.9 85.9	85.9	6.3 6.4	6.3		6.3	2.4 2.4		2.4	2.4		2.4	2.4	3.4 3.5	3.5
26-May-14	Sunny	Moderate	18:09	4.1	Surface	1.0	<u>27.8</u> 27.7	27.8	8.1 8.1	8.1	13.5 13.5	13.5	95.0 91.2	93.1	6.9 6.7	6.8	6.8	2.5 2.5	2.5	2.5	2.9 3.4	3.2	3.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.1	<u>27.5</u> 27.8	27.6	8.1 8.1	8.1	14.4 13.9	14.1	89.7 93.6	91.7	6.5 6.8	6.7		6.7	2.5 2.5		2.5	2.5		2.5	2.5	2.9 4.3	3.6
28-May-14	Sunny	Moderate	19:12	4.8	Surface	1.0	<u>27.8</u> 27.8	27.8	8.1 8.1	8.1	10.9 11.0	11.0	90.6 91.3	91.0	6.7 6.8	6.7	6.7	2.9 3.0	3.0	3.1	4.6 6.4	5.5	5.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.8	<u>27.6</u> 27.7	27.7	8.1 8.1	8.1	14.0 14.7	14.3	89.0 90.8	89.9	6.5 6.6	6.5		6.5	3.0 3.1		3.1	3.1		3.1	3.1	7.2 5.2	6.2
30-May-14	Sunny	Moderate	06:37	4.1	Surface	1.0	<u>27.0</u> 26.9	26.9	8.0 8.0	8.0	18.2 17.9	18.1	77.5 80.1	78.8	5.6 5.8	5.7	5.7	1.7 1.7	1.7	1.8	3.6 3.8	3.7	3.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.1	<u>26.9</u> 26.8	26.8	8.0 8.0	8.0	20.3 20.3	20.3	78.4 84.4	81.4	5.6 6.0	5.8		5.8	1.8 1.8		1.8	1.8		1.8	1.8	3.5 3.1	3.3

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10A - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	15:27	6.5	Surface	1.0	24.3 24.4	24.3	8.3 8.3	8.3	27.8 27.6	27.7	90.8 90.8	90.8	6.5 6.5	6.5	6.5	2.2 2.2	2.2	2.3	3.5 3.5	3.5	3.1
					Middle	3.3	24.1 24.1	24.1	8.3 8.3	8.3	28.4 28.4	28.4	90.1 90.0	90.1	6.4 6.4	6.4		2.2 2.1	2.2		2.2 2.5	2.5	
					Bottom	5.5	24.1 24.1	24.1	8.3 8.3	8.3	28.7 28.6	28.6	90.3 89.9	90.1	6.4 6.4	6.4		2.5 2.6	2.6		3.8 2.9	3.4	
5-May-14	Sunny	Moderate	17:26	6.3	Surface	1.0	24.0 24.0	24.0	8.5 8.5	8.5	29.4 29.8	29.6	93.6 92.7	93.2	6.7 6.6	6.6	6.6	1.4 1.5	1.5	1.4	4.4 3.0	3.7	3.9
					Middle	3.2	23.9 23.9	23.9	8.5 8.5	8.5	31.4 30.7	31.0	91.9 93.5	92.7	6.5 6.6	6.5		1.2 1.1	1.2		2.6 3.7	3.2	
					Bottom	5.3	23.9 23.9	23.9	8.4 8.5	8.5	31.9 32.0	31.9	95.8 92.6	94.2	6.7 6.5	6.6		1.3 1.4	1.4		4.7 4.6	4.7	
7-May-14	Cloudy	Moderate	18:58	6.5	Surface	1.0	23.6 23.6	23.6	8.4 8.4	8.4	31.3 31.4	31.4	99.4 90.1	94.8	7.0 6.4	6.7	6.6	1.9 1.8	1.9	2.0	5.3 4.9	5.1	4.6
					Middle	3.3	23.6 23.6	23.6	8.4 8.4	8.4	31.5 31.5	31.5	89.7 93.3	91.5	6.3 6.6	6.5		2.0 2.1	2.1		3.6 4.1	3.9	
					Bottom	5.5	23.6 23.5	23.6	8.4 8.4	8.4	31.5 31.6	31.5	89.2 91.9	90.6	6.6 6.5	6.4		2.0 2.1	2.1		5.2 4.3	4.8	
9-May-14	Rainy	Moderate	15:35	6.7	Surface	1.0	23.5 23.5	23.5	8.4 8.4	8.4	31.2 31.3	31.3	88.2 87.0	87.6	6.3 6.2	6.2	6.2	2.1 2.1	2.1	2.1	3.4 3.6	3.5	4.5
					Middle	3.4	23.5 23.5	23.5	8.4 8.4	8.4	31.4 31.3	31.4	87.0 88.8	87.9	6.2 6.3	6.2		2.1 2.1	2.1		5.0 4.9	5.0	
					Bottom	5.7	23.5 23.5	23.5	8.4 8.4	8.4	31.4 31.5	31.5	90.6 87.5	89.1	6.4 6.2	6.3		2.2 2.2	2.2		5.1 5.0	5.1	
12-May-14	Sunny	Moderate	10:37	6.2	Surface	1.0	23.8 23.8	23.8	8.3 8.3	8.3	22.7 22.7	22.7	93.3 87.2	90.3	6.9 6.4	6.6	6.6	3.4 3.4	3.4	3.4	5.7 4.0	4.9	4.9
					Middle	3.1	23.8 23.8	23.8	8.3 8.3	8.3	23.9 23.6	23.8	86.9 88.4	87.7	6.4 6.5	6.5		3.4 3.4	3.4		3.6 4.7	4.2	
					Bottom	5.2	23.8 23.8	23.8	8.3 8.3	8.3	24.4 24.0	24.2	87.7 86.7	87.2	6.5 6.4	6.5		3.6 3.4	3.5		5.7 5.6	5.7	
14-May-14	Sunny	Moderate	11:39	6.4	Surface	1.0	24.9 24.7	24.8	7.7 7.7	7.7	21.4 22.4	21.9	86.5 85.8	86.2	6.3 6.3	6.3	6.3	3.7 3.6	3.7	3.6	4.0 4.0	4.0	4.3
					Middle	3.2	24.7 24.6	24.6	7.7 7.7	7.7	22.7 23.1	22.9	85.8 85.2	85.5	6.3 6.2	6.2		3.6 3.5	3.6		3.1 5.3	4.2	
					Bottom	5.4	24.7 24.6	24.7	7.7 7.7	7.7	22.7 23.4	23.0	85.7 85.2	85.5	6.3 6.2	6.2		3.6 3.5	3.6		3.8 5.4	4.6	
16-May-14	Cloudy	Moderate	14:54	6.7	Surface	1.0	25.5 25.4	25.5	7.6 7.7	7.7	20.2 20.2	20.2	85.1 84.1	84.6	6.2 6.2	6.2	6.2	5.0 5.2	5.1	5.3	4.4 3.5	4.0	5.4
					Middle	3.4	25.3 25.4	25.4	7.7 7.6	7.7	21.2 20.4	20.8	83.8 85.1	84.5	6.1 6.2	6.2		5.3 5.3	5.3		5.8 6.4	6.1	
					Bottom	5.7	25.4 25.3	25.3	7.7 7.6	7.6	21.4 20.7	21.0	84.2 86.7	85.5	6.1 6.3	6.2		5.5 5.5	5.5		6.2 6.0	6.1	
19-May-14	Sunny	Rough	16:51	6.6	Surface	1.0	26.7 26.5	26.6	7.4 7.5	7.5	15.4 15.7	15.5	83.4 81.4	82.4	6.1 6.0	6.1	6.1	3.4 3.4	3.4	3.4	4.1 3.9	4.0	4.3
					Middle	3.3	26.4 26.5	26.5	7.5 7.4	7.5	16.2 16.3	16.2	81.8 83.7	82.8	6.0 6.1	6.1		3.3 3.3	3.3		4.1 4.3	4.2	
					Bottom	5.6	26.5 26.6	26.5	7.5 7.4	7.4	16.2 16.2	16.2	82.5 86.8	84.7	6.1 6.4	6.2		3.5 3.4	3.5		4.6 4.6	4.6	
21-May-14	Cloudy	Moderate	18:51	6.4	Surface	1.0	26.6 26.6	26.6	7.6 7.6	7.6	16.9 16.9	16.9	84.2 84.5	84.4	6.1 6.2	6.2	6.2	2.5 2.4	2.5	2.5	4.0 5.1	4.6	4.8
					Middle	3.2	26.6 26.6	26.6	7.6 7.6	7.6	17.0 17.0	17.0	84.5 83.9	84.2	6.2 6.1	6.1		2.5 2.5	2.5		4.6 5.3	5.0	
					Bottom	5.4	26.6 26.6	26.6	7.6 7.6	7.6	17.0 17.1	17.1	84.2 85.3	84.8	6.1 6.2	6.2		2.4 2.5	2.5		5.9 3.6	4.8	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10A - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	07:58	6.5	Surface	1.0	26.2 <u>26.2</u>	26.2	7.6 <u>7.6</u>	7.6	16.7 <u>16.9</u>	16.8	85.1 <u>84.8</u>	85.0	6.3 <u>6.2</u>	6.3	6.3	2.4 <u>2.3</u>	2.4	2.3	6.2 <u>5.1</u>	5.7	5.1
					Middle	3.3	26.2 <u>26.2</u>	26.2	7.6 <u>7.6</u>	7.6	17.2 <u>17.0</u>	17.1	85.1 <u>84.6</u>	84.9	6.3 <u>6.2</u>	6.2		2.2 <u>2.2</u>	2.2		5.0 <u>5.1</u>	5.1	
					Bottom	5.5	26.2 <u>26.2</u>	26.2	7.6 <u>7.6</u>	7.6	17.3 <u>17.3</u>	17.3	85.3 <u>84.6</u>	85.0	6.3 <u>6.2</u>	6.2		2.5 <u>2.3</u>	2.4		4.3 <u>4.8</u>	4.6	
26-May-14	Sunny	Moderate	10:35	6.6	Surface	1.0	27.2 <u>27.2</u>	27.2	7.5 <u>7.5</u>	7.5	13.8 <u>14.0</u>	13.9	85.5 <u>84.5</u>	85.0	6.3 <u>6.2</u>	6.2	6.2	3.4 <u>3.3</u>	3.4	3.9	4.4 <u>3.8</u>	4.1	4.7
					Middle	3.3	27.1 <u>27.2</u>	27.1	7.5 <u>7.5</u>	7.5	14.8 <u>14.0</u>	14.4	84.1 <u>85.9</u>	85.0	6.2 <u>6.3</u>	6.2		3.6 <u>3.8</u>	3.7		4.8 <u>5.2</u>	5.0	
					Bottom	5.6	27.1 <u>27.0</u>	27.1	7.5 <u>7.5</u>	7.5	15.0 <u>15.1</u>	15.0	85.0 <u>87.7</u>	86.4	6.2 <u>6.4</u>	6.3		4.5 <u>4.8</u>	4.7		5.1 <u>4.9</u>	5.0	
28-May-14	Sunny	Moderate	11:38	6.6	Surface	1.0	27.6 <u>27.6</u>	27.6	8.0 <u>8.1</u>	8.1	16.9 <u>17.1</u>	17.0	102.1 <u>101.5</u>	101.8	7.3 <u>7.3</u>	7.3	7.3	1.9 <u>1.9</u>	1.9	2.1	4.4 <u>2.5</u>	3.5	3.4
					Middle	3.3	27.5 <u>27.4</u>	27.5	8.0 <u>8.1</u>	8.0	17.2 <u>17.7</u>	17.5	101.1 <u>100.9</u>	101.0	7.3 <u>7.2</u>	7.2		2.2 <u>2.1</u>	2.2		2.8 <u>4.4</u>	3.6	
					Bottom	5.6	27.5 <u>27.6</u>	27.5	8.0 <u>8.0</u>	8.0	17.5 <u>18.0</u>	17.8	101.1 <u>102.1</u>	101.6	7.2 <u>7.3</u>	7.3		2.1 <u>2.2</u>	2.2		2.9 <u>3.5</u>	3.2	
30-May-14	Sunny	Moderate	14:05	6.3	Surface	1.0	28.0 <u>27.9</u>	28.0	8.4 <u>8.3</u>	8.4	18.3 <u>18.9</u>	18.6	104.2 <u>105.9</u>	105.1	7.4 <u>7.5</u>	7.4	7.4	1.5 <u>1.5</u>	1.5	1.6	4.1 <u>4.9</u>	4.5	4.2
					Middle	3.2	27.7 <u>27.8</u>	27.7	8.3 <u>8.4</u>	8.3	19.3 <u>19.2</u>	19.3	105.0 <u>101.8</u>	103.4	7.4 <u>7.2</u>	7.3		1.5 <u>1.6</u>	1.6		3.5 <u>4.9</u>	4.2	
					Bottom	5.3	28.0 <u>27.9</u>	28.0	8.4 <u>8.3</u>	8.4	19.2 <u>19.3</u>	19.2	100.6 <u>104.0</u>	102.3	7.1 <u>7.4</u>	7.2		1.6 <u>1.6</u>	1.6		4.4 <u>3.4</u>	3.9	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10A - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
2-May-14	Sunny	Moderate	06:55	6.6	Surface	1.0	23.8 23.8	23.8	8.4 8.4	8.4	26.7 26.7	26.7	88.8 89.0	88.9	6.4 6.5	6.5	6.5	2.4 2.3	2.4	2.4	3.9 3.3	3.6	3.4
					Middle	3.3	23.8 23.8	23.8	8.4 8.4	8.4	27.6 27.6	27.6	88.9 88.6	88.8	6.4 6.4	6.4		2.3 2.3	2.3		2.9 3.2	3.1	
					Bottom	5.6	23.8 23.8	23.8	8.4 8.4	8.4	28.1 28.1	28.1	88.8 88.8	88.8	6.4 6.4	6.4		2.4 2.3	2.4		3.3 3.4	3.4	
5-May-14	Sunny	Moderate	08:29	6.7	Surface	1.0	23.8 23.8	23.8	8.5 8.5	8.5	29.1 29.0	29.1	90.4 91.1	90.8	6.5 6.5	6.5	6.5	1.5 1.6	1.6	1.5	2.6 3.1	2.9	3.1
					Middle	3.4	23.9 23.9	23.9	8.5 8.5	8.5	29.9 29.6	29.8	90.6 91.7	91.2	6.4 6.5	6.5		1.3 1.4	1.4		3.6 3.0	3.3	
					Bottom	5.7	23.9 23.9	23.9	8.5 8.5	8.5	30.2 30.2	30.2	93.4 90.9	92.2	6.6 6.5	6.5		1.5 1.4	1.5		3.7 2.4	3.1	
7-May-14	Cloudy	Moderate	10:20	6.7	Surface	1.0	23.5 23.5	23.5	8.4 8.5	8.5	31.3 31.3	31.3	90.0 97.5	93.8	6.4 6.9	6.6	6.6	1.5 1.5	1.5	1.6	5.3 4.7	5.0	4.8
					Middle	3.4	23.5 23.5	23.5	8.5 8.5	8.5	31.4 31.4	31.4	89.1 93.2	91.2	6.3 6.6	6.5		1.6 1.6	1.6		4.3 4.6	4.5	
					Bottom	5.7	23.5 23.5	23.5	8.5 8.5	8.5	31.5 31.4	31.5	91.5 88.7	90.1	6.5 6.3	6.4		1.7 1.7	1.7		4.7 4.8	4.8	
9-May-14	Rainy	Moderate	08:48	6.4	Surface	1.0	23.5 23.5	23.5	8.4 8.4	8.4	31.7 31.7	31.7	84.0 84.9	84.5	5.9 6.0	6.0	6.0	2.7 2.7	2.7	2.8	4.2 5.3	4.8	5.5
					Middle	3.2	23.5 23.5	23.5	8.4 8.4	8.4	31.9 31.9	31.9	83.9 85.4	84.7	5.9 6.0	6.0		2.7 2.8	2.8		5.5 5.1	5.3	
					Bottom	5.4	23.5 23.5	23.5	8.4 8.3	8.3	31.9 31.9	31.9	84.4 89.5	87.0	6.0 6.3	6.2		2.7 2.8	2.8		6.3 6.3	6.3	
12-May-14	Sunny	Moderate	18:23	6.4	Surface	1.0	24.4 24.5	24.5	8.2 8.2	8.2	17.7 17.6	17.7	86.4 86.4	86.4	6.5 6.5	6.5	6.5	4.4 4.5	4.5	4.6	3.6 4.1	3.9	4.1
					Middle	3.2	24.2 24.2	24.2	8.2 8.2	8.2	20.7 20.4	20.6	85.2 86.1	85.7	6.3 6.4	6.4		4.5 4.6	4.6		4.6 4.0	4.3	
					Bottom	5.4	23.8 24.4	24.1	8.1 8.1	8.1	26.3 24.7	25.5	84.8 85.5	85.2	6.2 6.3	6.2		4.6 4.6	4.6		4.7 3.4	4.1	
14-May-14	Sunny	Moderate	20:22	6.5	Surface	1.0	24.7 24.7	24.7	7.7 7.7	7.7	21.8 22.1	22.0	82.8 83.6	83.2	6.1 6.1	6.1	6.1	5.2 5.4	5.3	6.2	5.4 4.6	5.0	4.9
					Middle	3.3	24.5 24.5	24.5	7.6 7.7	7.6	24.3 23.6	23.9	82.5 84.4	83.5	6.0 6.2	6.1		6.7 6.7	6.7		5.4 5.2	5.3	
					Bottom	5.5	24.6 24.5	24.5	7.7 7.6	7.7	25.0 24.9	24.9	82.8 85.6	84.2	6.0 6.2	6.1		6.7 6.6	6.7		4.8 4.2	4.5	
16-May-14	Cloudy	Moderate	06:15	6.3	Surface	1.0	25.2 25.0	25.1	7.7 7.7	7.7	21.2 19.8	20.5	82.4 82.3	82.4	6.0 6.1	6.0	6.0	4.3 4.5	4.4	4.8	3.4 3.7	3.6	4.1
					Middle	3.2	24.8 24.8	24.8	7.7 7.7	7.7	23.8 23.7	23.8	81.7 81.9	81.8	5.9 5.9	5.9		4.9 4.7	4.8		3.5 4.9	4.2	
					Bottom	5.3	24.8 24.8	24.8	7.7 7.7	7.7	24.1 24.0	24.1	81.5 82.0	81.8	5.9 5.9	5.9		5.1 5.4	5.3		4.9 4.3	4.6	
19-May-14	Cloudy	Moderate	08:34	6.5	Surface	1.0	26.1 26.0	26.0	7.5 7.5	7.5	15.7 15.8	15.7	77.0 76.5	76.8	5.7 5.7	5.7	5.7	3.1 3.1	3.1	3.0	3.3 3.4	3.4	3.5
					Middle	3.3	25.9 25.9	25.9	7.6 7.5	7.5	17.7 17.4	17.6	76.8 78.5	77.7	5.7 5.8	5.7		2.9 2.9	2.9		3.5 3.3	3.4	
					Bottom	5.5	25.8 25.9	25.9	7.5 7.5	7.5	18.1 17.9	18.0	80.4 76.3	78.4	5.9 5.6	5.8		2.9 2.8	2.9		3.4 3.7	3.6	
21-May-14	Cloudy	Moderate	10:29	6.5	Surface	1.0	26.1 26.1	26.1	7.6 7.6	7.6	14.9 14.8	14.9	80.6 81.2	80.9	6.0 6.1	6.0	6.0	3.0 3.0	3.0	3.2	4.3 4.2	4.3	5.4
					Middle	3.3	25.9 25.9	25.9	7.6 7.7	7.7	17.4 16.0	16.7	79.8 80.8	80.3	5.9 6.0	5.9		3.2 3.3	3.3		5.2 5.5	5.4	
					Bottom	5.5	25.9 26.0	25.9	7.6 7.6	7.6	21.1 20.3	20.7	82.8 80.3	81.6	6.0 5.8	5.9		3.3 3.4	3.4		6.6 6.5	6.6	

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10A - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)				
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*	
23-May-14	Cloudy	Moderate	15:09	6.9	Surface	1.0	26.2 26.1	26.1	7.6 7.6	7.6	15.7 15.3	15.5	82.6 81.2	81.9	6.1 6.0	6.1	6.0	2.9 2.6	2.8	2.8	2.4 3.5	3.0	2.8
					Middle	3.5	25.8 25.8	25.8	7.7 7.6	7.6	20.6 20.5	20.6	78.5 80.7	79.6	5.7 5.9	5.8		2.8 2.5	2.7		2.4 2.4	2.4	
					Bottom	5.9	25.8 25.8	25.8	7.6 7.6	7.6	20.6 20.7	20.7	83.1 79.0	81.1	6.0 5.7	5.9		3.0 2.8	2.9		2.8 3.0	2.9	
26-May-14	Sunny	Moderate	19:07	6.3	Surface	1.0	26.4 26.4	26.4	7.6 7.7	7.6	22.8 22.7	22.8	76.9 76.7	76.8	5.4 5.4	5.4	5.4	3.0 3.1	3.1	3.4	2.6 2.9	2.8	3.3
					Middle	3.2	26.2 26.2	26.2	7.7 7.6	7.6	23.6 23.3	23.4	74.3 75.2	74.8	5.3 5.3	5.3		3.4 3.2	3.3		3.4 3.5	3.5	
					Bottom	5.3	25.6 25.6	25.6	7.5 7.6	7.6	26.0 26.1	26.0	76.3 70.2	73.3	5.4 5.0	5.2		3.8 3.8	3.8		3.8 3.6	3.7	
28-May-14	Sunny	Moderate	20:38	6.6	Surface	1.0	27.1 26.9	27.0	8.3 8.3	8.3	19.9 20.6	20.2	84.8 84.4	84.6	6.0 6.0	6.0	6.0	2.2 2.3	2.3	2.3	2.2 2.2	2.2	2.6
					Middle	3.3	26.8 26.7	26.8	8.3 8.3	8.3	21.2 21.5	21.3	84.7 82.8	83.8	6.0 5.9	5.9		2.2 2.3	2.3		2.2 2.1	2.2	
					Bottom	5.6	26.7 26.7	26.7	8.3 8.3	8.3	22.1 22.5	22.3	86.2 82.8	84.5	6.1 5.9	6.0		2.2 2.3	2.3		3.7 3.0	3.4	
30-May-14	Sunny	Moderate	05:54	6.1	Surface	1.0	26.8 26.9	26.9	8.4 8.4	8.4	18.7 18.9	18.8	80.5 79.8	80.2	5.8 5.7	5.8	5.7	1.1 1.1	1.1	1.2	2.9 3.0	3.0	3.1
					Middle	3.1	26.5 26.4	26.5	8.3 8.3	8.3	23.8 24.0	23.9	80.0 77.6	78.8	5.6 5.5	5.5		1.3 1.1	1.2		2.4 3.3	2.9	
					Bottom	5.1	26.8 26.4	26.6	8.3 8.3	8.3	23.8 24.2	24.0	79.5 77.4	78.5	5.6 5.4	5.5		1.3 1.2	1.3		2.8 3.9	3.4	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10B(N) - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
2-May-14	Sunny	Moderate	15:39	5.5	Surface	1.0	24.4 24.3	24.3	8.3 8.3	8.3	27.6 27.8	27.7	91.1 90.8	91.0	6.5 6.5	6.5	6.5	2.6 2.5	2.6	2.7	3.3 3.0	3.2	3.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.5	24.3 24.3	24.3	8.3 8.3	8.3	27.9 27.8	27.8	90.7 91.0	90.9	6.5 6.5	6.5		2.6 2.8	2.7		4.4 2.8	3.6					
5-May-14	Sunny	Moderate	17:42	5.3	Surface	1.0	23.9 24.0	24.0	8.4 8.4	8.4	30.4 30.3	30.4	91.9 91.6	91.8	6.5 6.5	6.5	6.5	1.3 1.4	1.4	1.4	2.9 3.3	3.1	2.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.3	23.9 23.9	23.9	8.4 8.4	8.4	31.3 31.5	31.4	91.4 91.0	91.2	6.5 6.4	6.4		1.4 1.4	1.4		2.3 2.3	2.3					
7-May-14	Cloudy	Moderate	19:11	4.9	Surface	1.0	23.6 23.6	23.6	8.4 8.4	8.4	31.4 31.4	31.4	87.9 88.1	88.0	6.2 6.2	6.2	6.2	1.7 1.7	1.7	1.8	4.7 4.4	4.6	4.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.9	23.6 23.6	23.6	8.4 8.3	8.4	31.4 31.5	31.5	87.9 88.0	88.0	6.2 6.2	6.2		1.7 1.8	1.8		5.8 4.2	5.0					
9-May-14	Rainy	Moderate	15:46	5.4	Surface	1.0	23.5 23.5	23.5	8.4 8.4	8.4	31.2 31.3	31.3	86.9 86.7	86.8	6.2 6.2	6.2	6.2	2.1 2.1	2.1	2.1	6.2 6.1	6.2	6.8				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-		
					Bottom	4.4	23.5 23.5	23.5	8.4 8.3	8.4	31.3 31.4	31.4	86.7 86.6	86.7	6.2 6.1	6.1		2.1 2.0	2.1		7.0 7.8	7.4					
12-May-14	Sunny	Moderate	10:31	4.8	Surface	1.0	23.8 23.8	23.8	8.2 8.2	8.2	23.8 24.0	23.9	89.3 87.5	88.4	6.6 6.4	6.5	6.5	3.5 3.6	3.6	3.6	3.9 4.3	4.1	3.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-			
					Bottom	3.8	23.8 23.8	23.8	8.2 8.1	8.2	24.3 24.6	24.5	86.9 88.2	87.6	6.4 6.5	6.5		3.6 3.6	3.6		3.3 3.3	3.3					
14-May-14	Sunny	Moderate	11:31	4.9	Surface	1.0	25.0 24.9	25.0	7.7 7.7	7.7	20.9 21.0	20.9	87.9 87.8	87.9	6.5 6.5	6.5	6.5	3.7 3.7	3.7	3.8	6.7 6.7	6.7	6.5				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-			
					Bottom	3.9	24.7 24.8	24.7	7.7 7.7	7.7	22.6 23.0	22.8	88.1 87.3	87.7	6.4 6.4	6.4		3.8 3.8	3.8		5.8 6.8	6.3					
16-May-14	Cloudy	Moderate	15:06	5.1	Surface	1.0	25.5 25.4	25.4	7.7 7.6	7.7	20.3 20.4	20.4	84.3 84.1	84.2	6.2 6.1	6.2	6.2	4.8 4.7	4.8	4.8	4.3 5.6	5.0	5.3				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-			
					Bottom	4.1	25.4 25.4	25.4	7.7 7.6	7.6	20.5 20.7	20.6	84.2 83.9	84.1	6.1 6.1	6.1		4.8 4.7	4.8		5.8 5.2	5.5					
19-May-14	Sunny	Rough	17:02	4.9	Surface	1.0	26.7 26.6	26.7	7.5 7.5	7.5	15.5 16.7	16.1	83.6 84.1	83.9	6.1 6.2	6.1	6.1	3.5 3.4	3.5	3.5	2.9 2.7	2.8	4.0				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-			
					Bottom	3.9	26.8 26.6	26.7	7.5 7.5	7.5	16.4 16.7	16.6	85.1 83.2	84.2	6.2 6.1	6.2		3.4 3.6	3.5		5.5 4.9	5.2					
21-May-14	Cloudy	Moderate	19:02	5.1	Surface	1.0	26.6 26.6	26.6	7.6 7.6	7.6	17.1 17.1	17.1	83.5 83.7	83.6	6.1 6.1	6.1	6.1	2.2 2.2	2.2	2.3	3.9 4.2	4.1	3.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-			
					Bottom	4.1	26.6 26.6	26.6	7.6 7.5	7.6	17.1 17.1	17.1	83.5 83.5	83.5	6.1 6.1	6.1		2.3 2.3	2.3		2.7 3.8	3.3					

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10B(N) - Mid-EbbTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	07:43	5.0	Surface	1.0	25.9 <u>25.9</u>	25.9	7.5 <u>7.6</u>	7.6	19.3 <u>19.3</u>	19.3	83.6 <u>82.5</u>	83.1	6.1 <u>6.0</u>	6.1	6.1	2.5 <u>2.5</u>	2.5	2.5	4.1 <u>4.9</u>	4.5	4.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.0	25.9 <u>25.9</u>	25.9	7.6 <u>7.5</u>	7.5	19.7 <u>19.8</u>	19.7	82.6 <u>85.4</u>	84.0	6.0 <u>6.2</u>	6.1		6.1	2.5 <u>2.3</u>		2.4	2.5		2.4	4.0 <u>4.4</u>	4.2	
26-May-14	Sunny	Moderate	10:19	5.3	Surface	1.0	26.8 <u>26.8</u>	26.8	7.5 <u>7.5</u>	7.5	16.6 <u>17.8</u>	17.2	80.5 <u>79.4</u>	80.0	5.9 <u>5.8</u>	5.8	5.8	3.6 <u>3.4</u>	3.5	3.6	3.1 <u>2.9</u>	3.0	3.9				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.3	26.5 <u>26.3</u>	26.4	7.5 <u>7.6</u>	7.5	19.8 <u>19.6</u>	19.7	80.3 <u>78.0</u>	79.2	5.8 <u>5.6</u>	5.7		5.7	3.6 <u>3.5</u>		3.6	3.6		4.9 <u>4.7</u>	4.8		
28-May-14	Sunny	Moderate	11:32	4.8	Surface	1.0	27.0 <u>27.0</u>	27.0	7.7 <u>7.7</u>	7.7	20.2 <u>20.6</u>	20.4	92.3 <u>94.2</u>	93.3	6.6 <u>6.7</u>	6.6	6.6	2.1 <u>2.0</u>	2.1	2.1	3.0 <u>3.3</u>	3.2	3.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.8	26.8 <u>27.0</u>	26.9	7.6 <u>7.6</u>	7.6	21.3 <u>20.6</u>	21.0	91.1 <u>93.7</u>	92.4	6.5 <u>6.7</u>	6.6		6.6	2.2 <u>2.0</u>		2.1	2.1		3.4 <u>3.0</u>	3.2		
30-May-14	Sunny	Moderate	14:12	4.8	Surface	1.0	27.8 <u>27.7</u>	27.7	8.3 <u>8.3</u>	8.3	19.1 <u>19.3</u>	19.2	103.7 <u>102.5</u>	103.1	7.3 <u>7.2</u>	7.3	7.3	1.5 <u>1.5</u>	1.5	1.6	4.4 <u>2.4</u>	3.4	3.6				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.8	27.8 <u>27.6</u>	27.7	8.3 <u>8.2</u>	8.3	19.1 <u>19.6</u>	19.4	102.9 <u>102.2</u>	102.6	7.3 <u>7.2</u>	7.2		7.2	1.5 <u>1.7</u>		1.6	1.6		4.1 <u>3.5</u>	3.8		

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10B(N) - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)							
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*				
2-May-14	Sunny	Moderate	06:46	5.6	Surface	1.0	23.6 23.6	23.6	8.4 8.4	8.4	30.5 30.5	30.5	87.3 87.4	87.4	6.2 6.2	6.2	6.2	2.3 2.2	2.3	2.4	4.4 4.5	4.5	4.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-
					Bottom	4.6	23.6 23.6	23.6	8.4 8.4	8.4	30.5 30.5	30.5	87.4 87.2	87.3	6.2 6.2	6.2		2.5 2.4	2.5		6.2	2.5 2.4		2.5	3.3 3.6	3.5
5-May-14	Sunny	Moderate	08:13	5.3	Surface	1.0	23.8 23.8	23.8	8.5 8.5	8.5	30.5 30.8	30.6	92.4 90.4	91.4	6.6 6.4	6.5	6.5	1.4 1.4	1.4	1.6	3.2 2.7	3.0	2.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.3	23.8 23.8	23.8	8.5 8.5	8.5	31.0 31.5	31.3	95.1 91.0	93.1	6.7 6.4	6.6		1.8 1.7	1.8		6.6	1.8 1.7		1.8	3.2 2.3	2.8
7-May-14	Cloudy	Moderate	10:16	5.0	Surface	1.0	23.6 23.6	23.6	8.5 8.5	8.5	31.6 31.7	31.6	86.2 87.1	86.7	6.1 6.2	6.1	6.1	1.7 1.9	1.8	1.8	6.1 5.9	6.0	5.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.0	23.6 23.6	23.6	8.5 8.5	8.5	31.7 31.7	31.7	86.1 86.2	86.2	6.1 6.1	6.1		1.9 1.7	1.8		6.1	1.9 1.7		1.8	4.7 5.0	4.9
9-May-14	Rainy	Moderate	08:43	5.0	Surface	1.0	23.5 23.5	23.5	8.3 8.3	8.3	31.4 31.4	31.4	84.1 85.1	84.6	6.0 6.0	6.0	6.0	2.9 2.9	2.9	3.0	4.0 4.4	4.2	5.6			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.0	23.5 23.5	23.5	8.3 8.3	8.3	31.5 31.4	31.5	84.5 86.9	85.7	6.0 6.2	6.1		3.0 3.0	3.0		6.1	3.0 3.0		3.0	7.2 6.8	7.0
12-May-14	Sunny	Moderate	18:30	5.0	Surface	1.0	24.5 24.0	24.3	8.2 8.2	8.2	18.2 18.6	18.4	87.0 86.7	86.9	6.5 6.5	6.5	6.5	3.9 3.9	3.9	4.0	4.5 3.7	4.1	4.0			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.0	24.3 24.1	24.2	8.2 8.1	8.1	22.8 24.1	23.4	86.0 85.9	86.0	6.3 6.4	6.3		4.0 4.1	4.1		6.3	4.0 4.1		4.1	4.2 3.3	3.8
14-May-14	Sunny	Moderate	20:28	5.4	Surface	1.0	24.5 24.6	24.5	7.7 7.7	7.7	21.7 21.6	21.6	81.8 82.2	82.0	6.0 6.1	6.0	6.0	6.8 6.8	6.8	6.7	4.0 3.2	3.6	3.5			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.4	24.5 24.2	24.4	7.7 7.6	7.7	25.0 26.4	25.7	81.8 81.4	81.6	5.9 5.9	5.9		6.5 6.5	6.5		5.9	6.5 6.5		6.5	3.8 2.7	3.3
16-May-14	Cloudy	Moderate	06:09	5.3	Surface	1.0	24.3 24.2	24.3	7.7 7.7	7.7	27.6 28.4	28.0	82.4 81.9	82.2	5.9 5.8	5.9	5.9	10.8 10.9	10.9	10.8	5.0 5.2	5.1	5.1			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.3	24.2 24.2	24.2	7.7 7.7	7.7	28.1 28.8	28.5	83.3 81.7	82.5	5.9 5.8	5.9		10.6 10.8	10.7		5.9	10.6 10.8		10.7	4.9 5.2	5.1
19-May-14	Cloudy	Moderate	08:30	5.2	Surface	1.0	25.7 25.8	25.8	7.6 7.6	7.6	17.2 16.7	17.0	79.1 79.8	79.5	5.9 5.9	5.9	5.9	3.3 3.2	3.3	3.3	4.0 4.4	4.2	4.9			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.2	25.5 25.4	25.4	7.6 7.6	7.6	25.2 24.8	25.0	80.6 78.2	79.4	5.8 5.6	5.7		3.2 3.3	3.3		5.7	3.2 3.3		3.3	5.6 5.3	5.5
21-May-14	Cloudy	Moderate	10:18	5.3	Surface	1.0	25.9 25.9	25.9	7.7 7.7	7.7	16.1 16.1	16.1	80.3 80.6	80.5	6.0 6.0	6.0	6.0	2.7 2.8	2.8	2.8	4.0 4.3	4.2	4.2			
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	
					Bottom	4.3	25.8 25.7	25.7	7.6 7.7	7.7	19.6 20.0	19.8	80.1 81.3	80.7	5.8 5.9	5.9		2.7 2.8	2.8		5.9	2.7 2.8		2.8	3.2 4.9	4.1

Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher

*** Cancelled due to Thunderstorm Warning and safety concern.

Appendix J - Marine Water Quality Monitoring Results

Water Quality Monitoring Results at SR10B(N) - Mid-FloodTide

Date	Weather Condition	Sea Condition**	Sampling Time	Water Depth (m)	Sampling Depth (m)	Temperature (°C)		pH		Salinity (ppt)		DO Saturation (%)		Dissolved Oxygen (mg/L)		Turbidity(NTU)			Suspended Solids (mg/L)								
						Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	DA*	Value	Average	DA*	Value	Average	DA*					
23-May-14	Cloudy	Moderate	15:26	5.3	Surface	1.0	26.2 26.1	26.2	7.6 7.6	7.6	14.9 15.1	15.0	81.9 79.6	80.8	6.1 5.9	6.0	6.0	2.9 2.9	2.9	2.9	2.6 3.0	2.8	2.7				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	-
					Bottom	4.3	25.7 25.8	25.8	7.6 7.6	7.6	21.0 21.0	21.0	77.7 79.4	78.6	5.6 5.7	5.7		5.7	2.7 2.8		2.8	2.7		2.8	3.1 2.1	2.6	
26-May-14	Sunny	Moderate	19:21	5.6	Surface	1.0	26.4 26.3	26.4	7.7 7.7	7.7	22.5 21.5	22.0	74.8 74.2	74.5	5.3 5.3	5.3	5.3	3.3 3.2	3.3	3.4	2.9 2.5	2.7	3.1				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.6	25.8 25.9	25.9	7.6 7.7	7.6	25.5 25.6	25.6	73.6 73.6	73.6	5.2 5.2	5.2		5.2	3.3 3.5		3.4	3.3		3.4	3.1 3.6	3.4	
28-May-14	Sunny	Moderate	20:47	5.2	Surface	1.0	26.9 26.9	26.9	8.3 8.3	8.3	20.7 20.8	20.7	82.3 82.2	82.3	5.9 5.8	5.8	5.8	2.0 1.9	2.0	2.0	2.9 2.5	2.7	3.2				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	4.2	26.7 26.7	26.7	8.3 8.2	8.2	21.9 21.8	21.9	81.8 81.6	81.7	5.8 5.8	5.8		5.8	1.9 1.9		1.9	1.9		1.9	2.8 4.4	3.6	
30-May-14	Sunny	Moderate	05:48	4.8	Surface	1.0	27.1 27.1	27.1	8.3 8.3	8.3	18.6 21.0	19.8	89.8 83.6	86.7	6.3 5.9	6.1	6.1	1.1 1.1	1.1	1.2	2.9 3.7	3.3	3.4				
					Middle	-	-	-	-	-	-	-	-	-	-	-		-	-		-	-		-	-	-	
					Bottom	3.8	26.6 26.6	26.6	8.3 8.4	8.4	23.7 23.2	23.5	81.8 84.1	83.0	5.8 6.0	5.9		5.9	1.1 1.2		1.2	1.1		1.2	2.5 4.4	3.5	

Remarks:

Bolded values means the measured values exceed the Action Level; Underlined bolded values means the measured values exceed the Limit Level.


Remarks:

* DA: Depth-Averaged

** Calm: Small or no wave; Moderate: Between calm and rough; Rough: White capped or rougher




*** Cancelled due to Thunderstorm Warning and safety concern.

Dissolved Oxygen (Bottom) at Mid-Ebb Tide

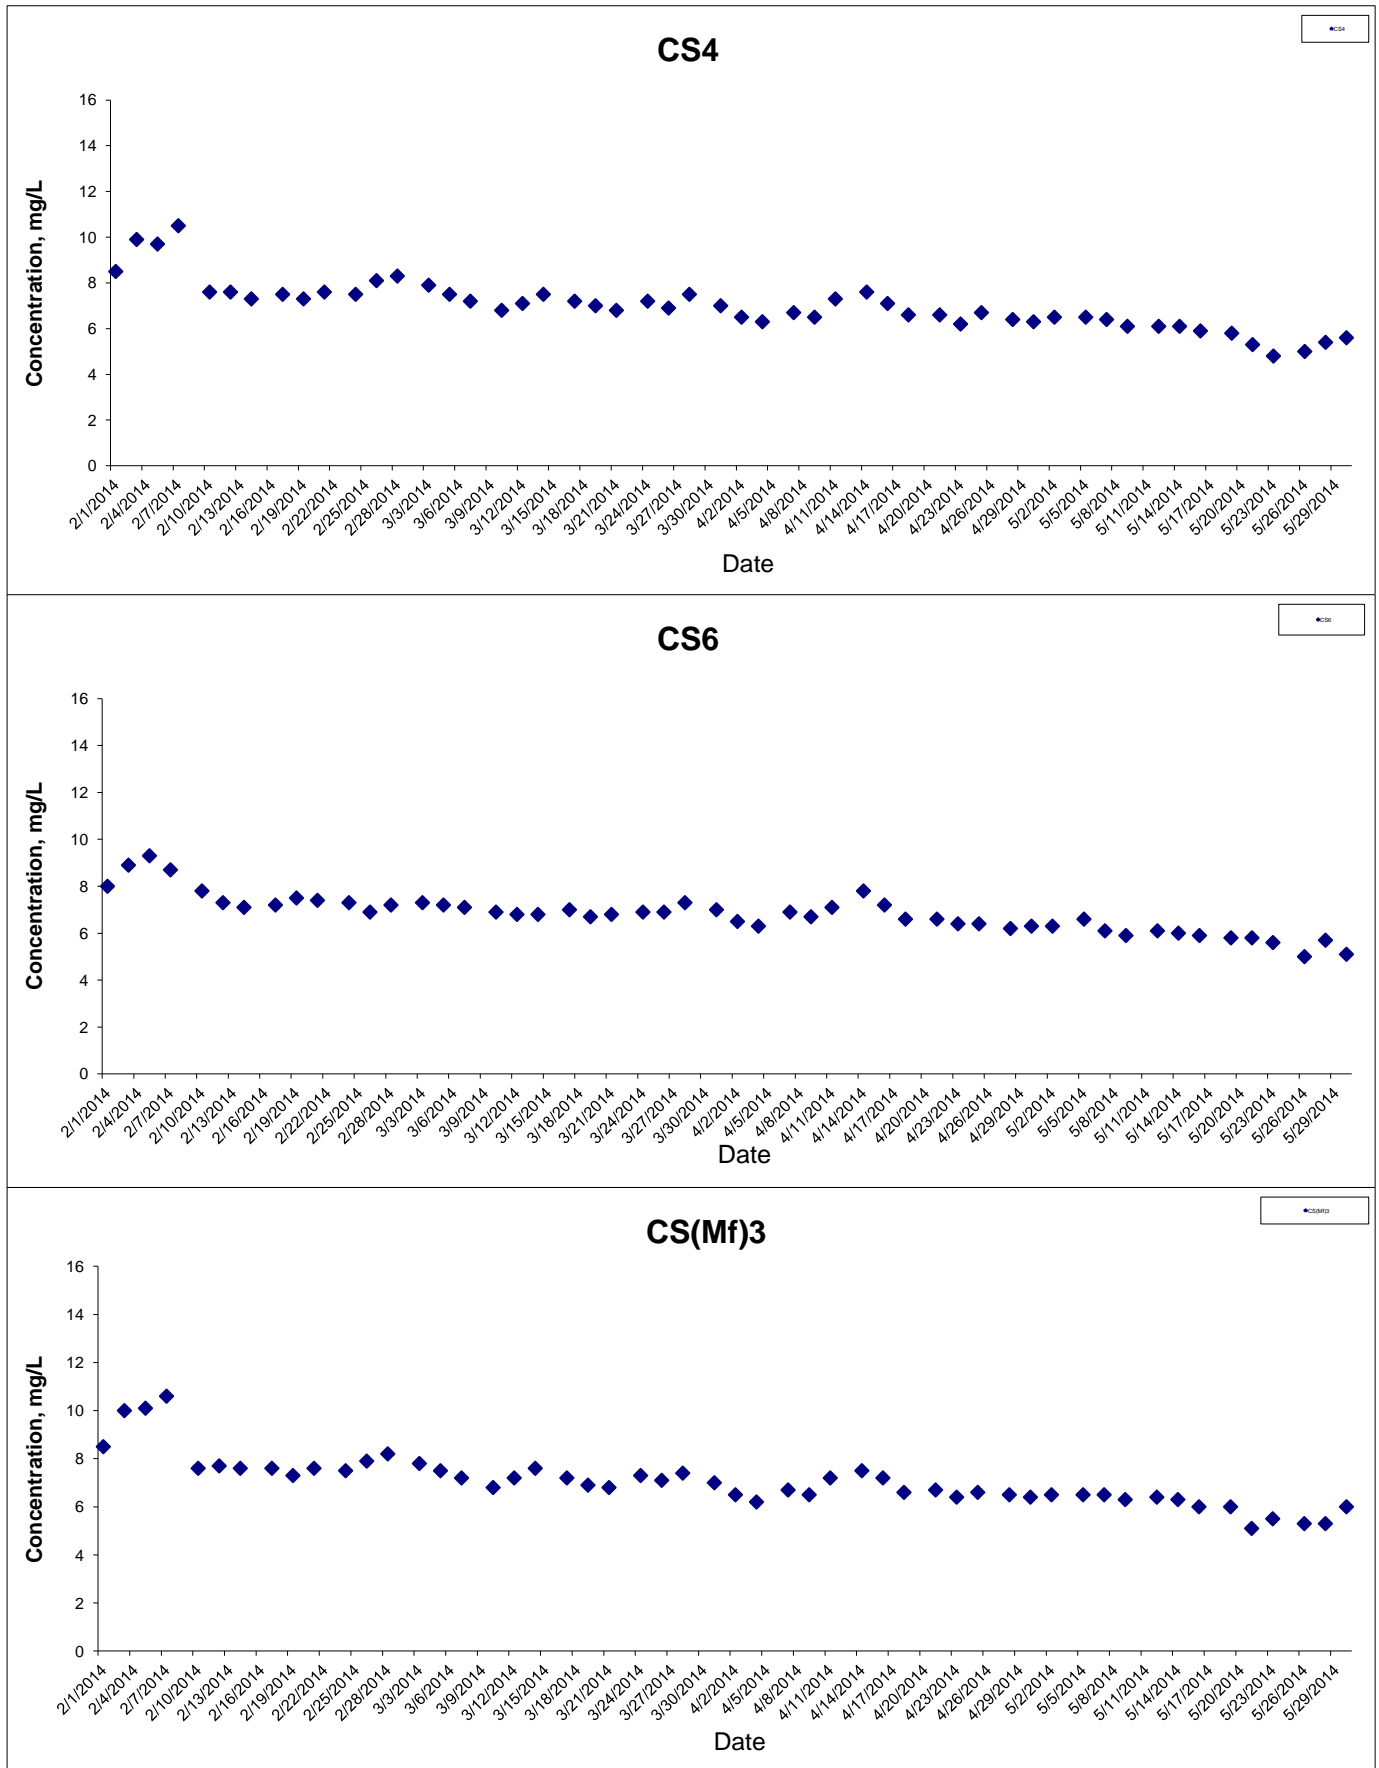

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Ebb Tide

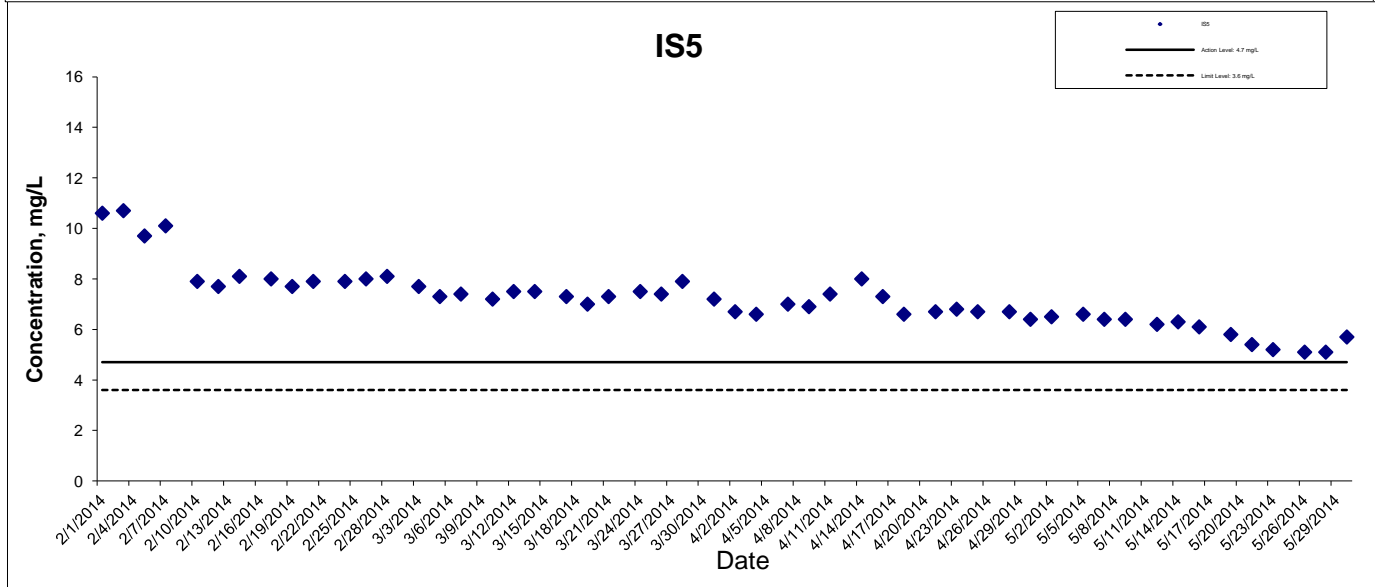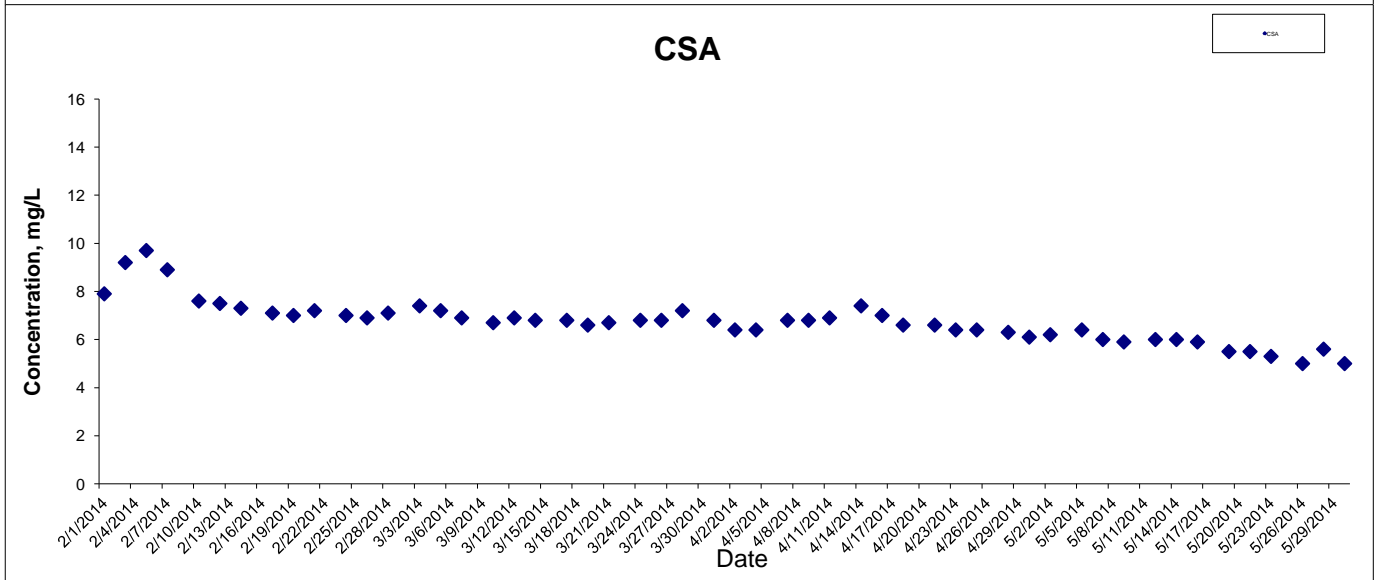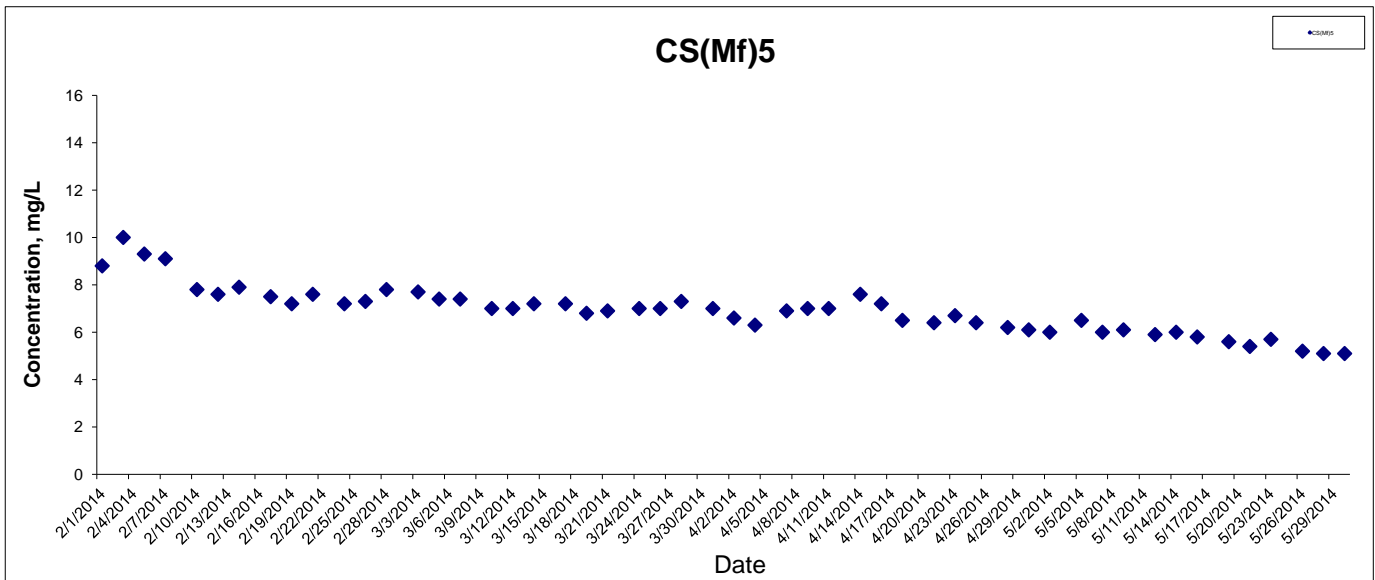




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

**Graphical Presentation of Impact Water Quality
 Monitoring Results**






Dissolved Oxygen (Bottom) at Mid-Ebb Tide

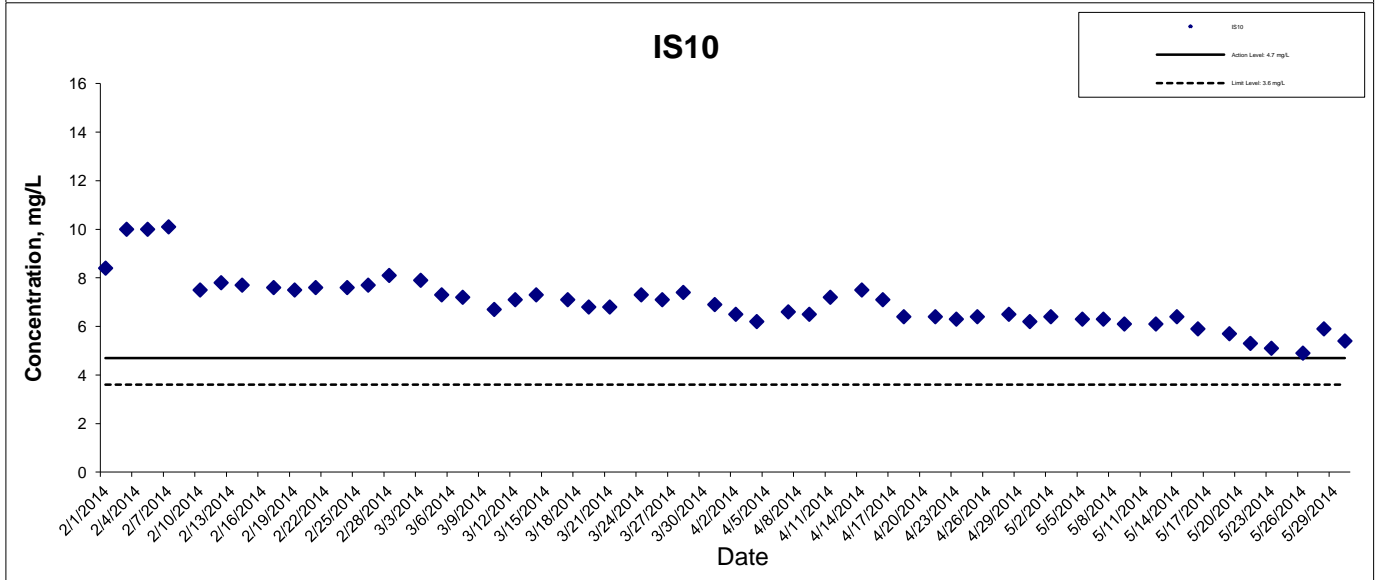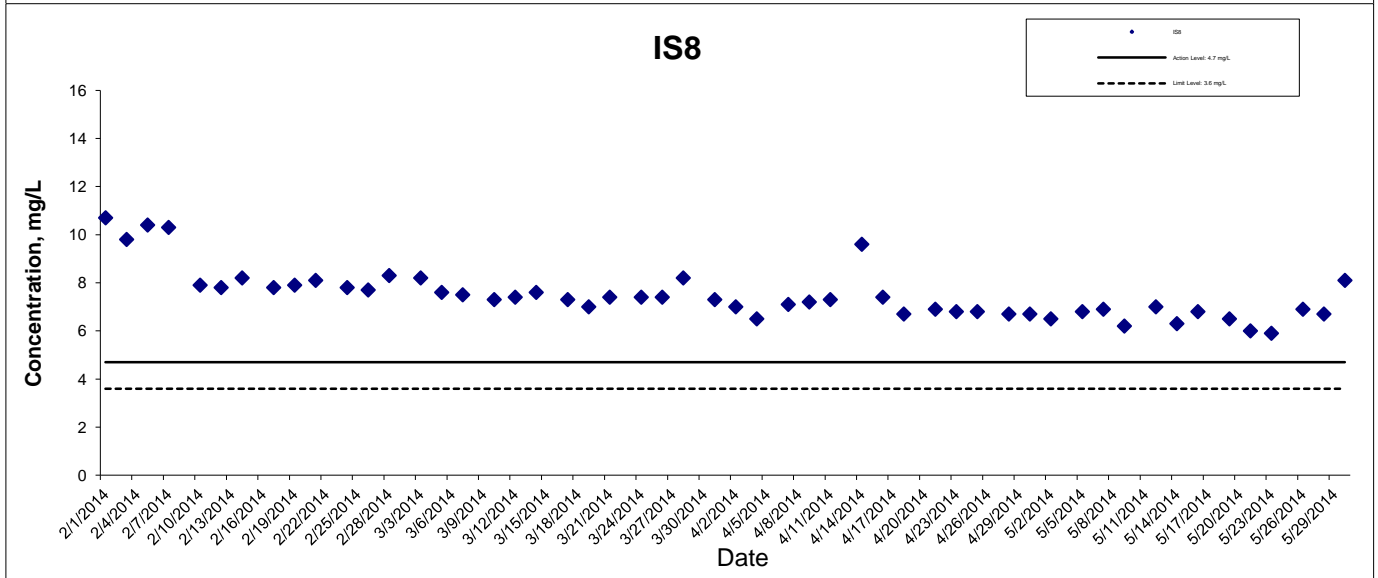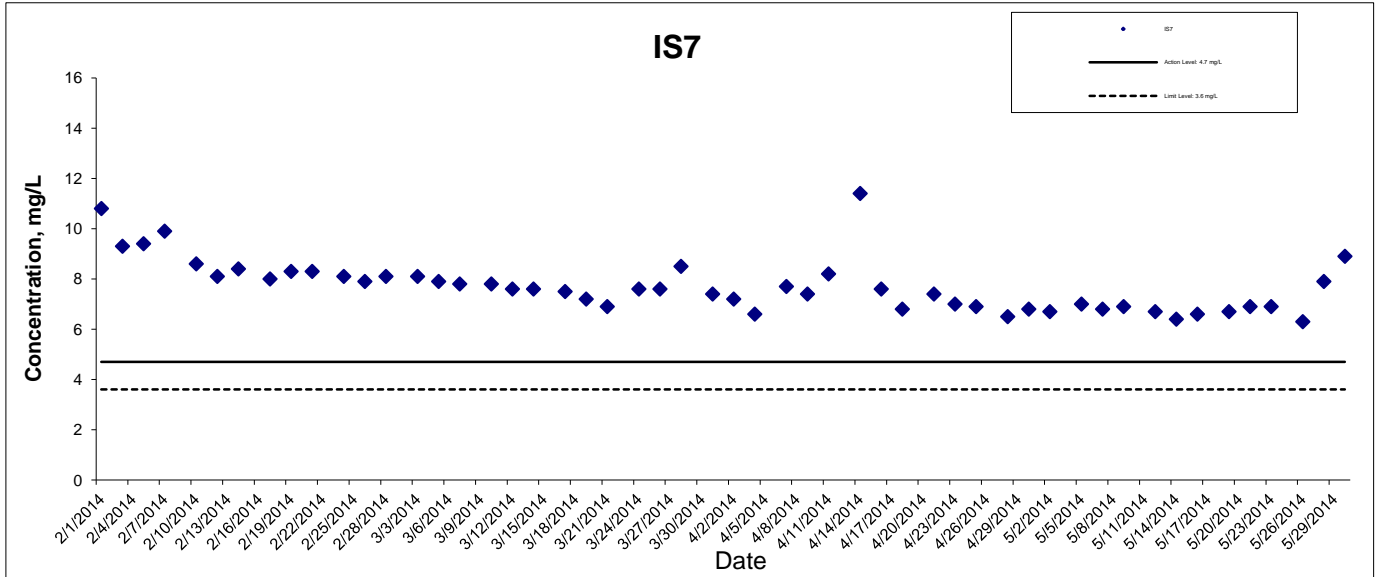




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Ebb Tide

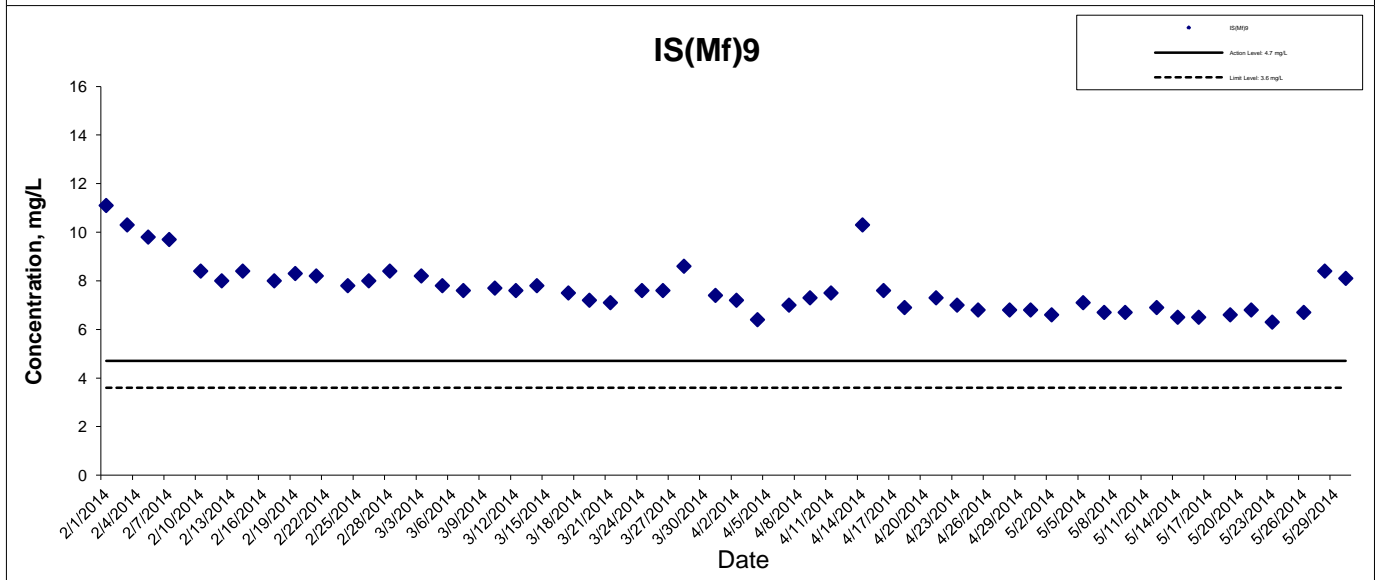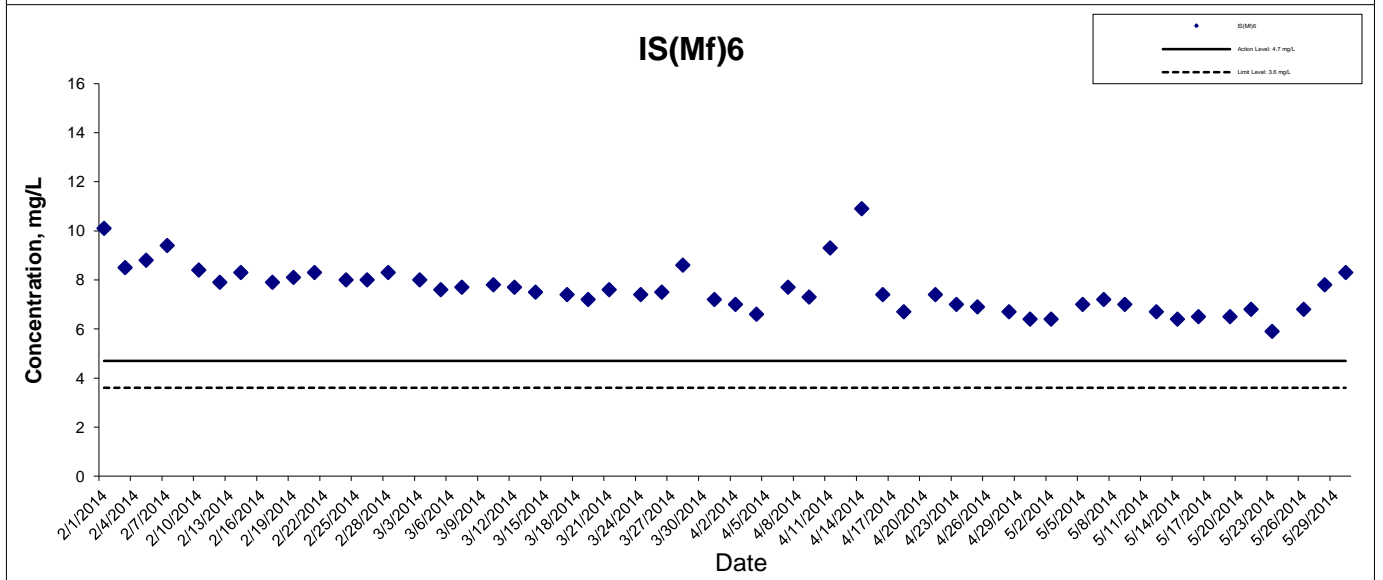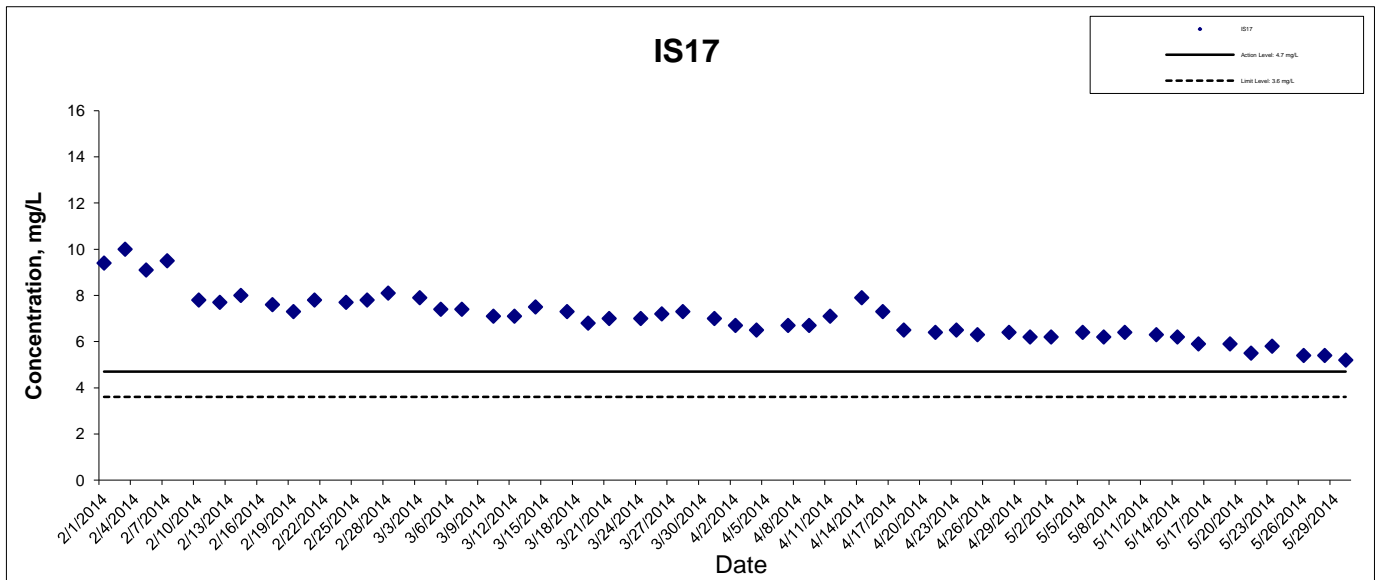




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Ebb Tide

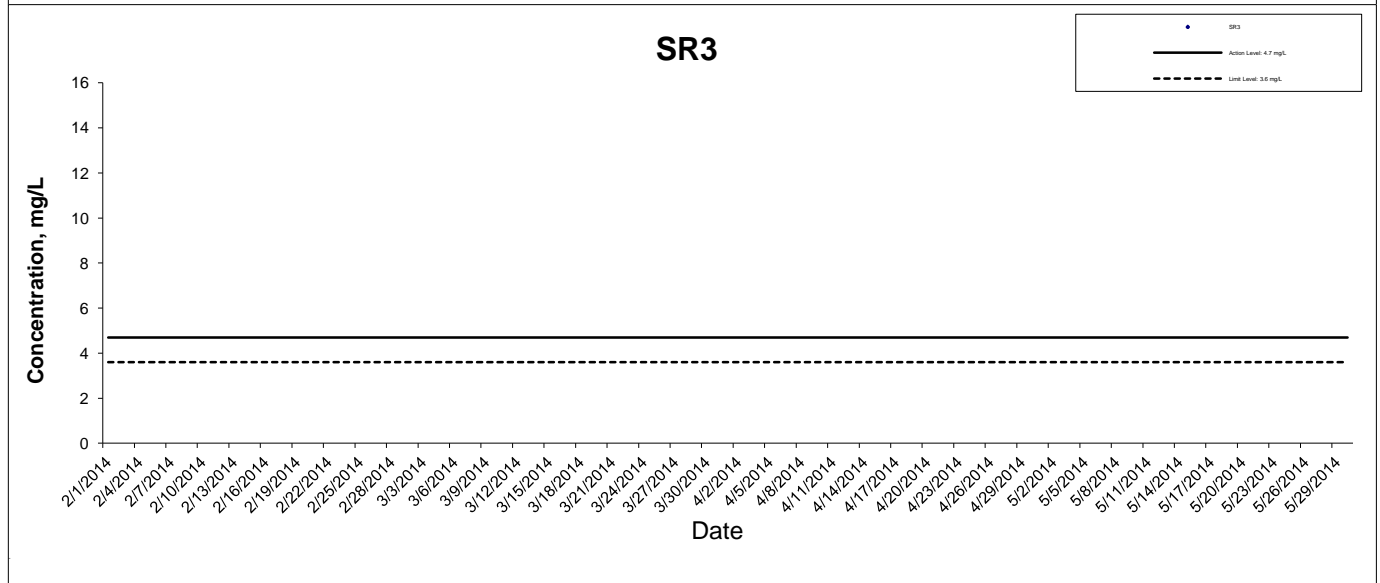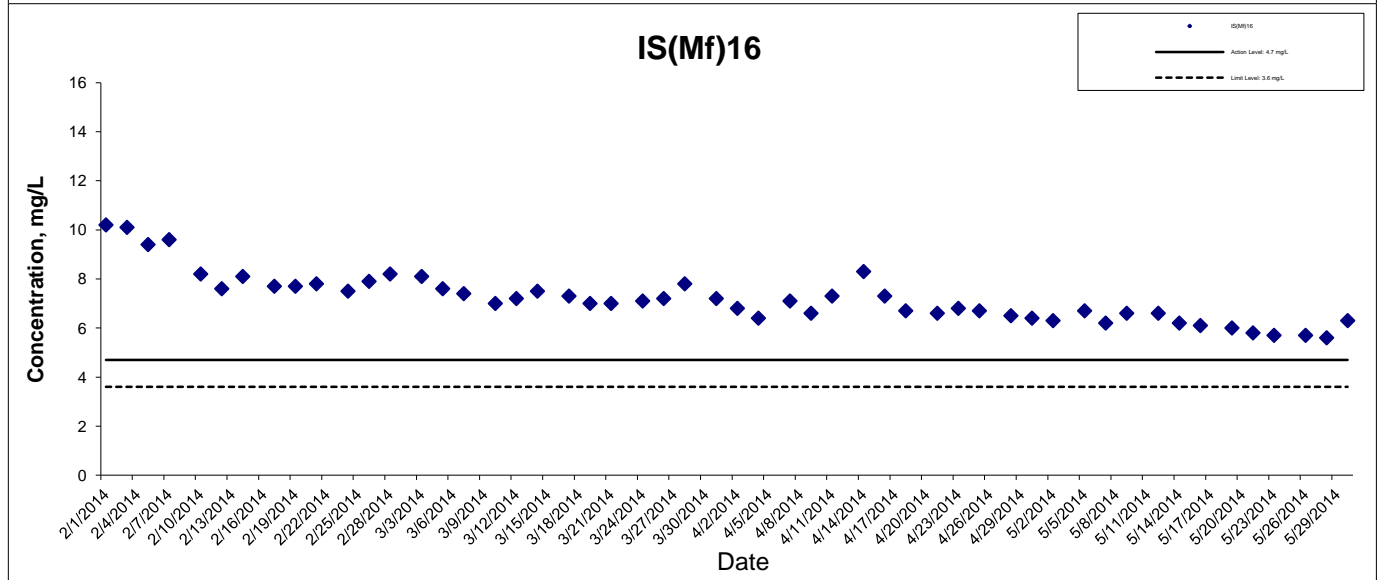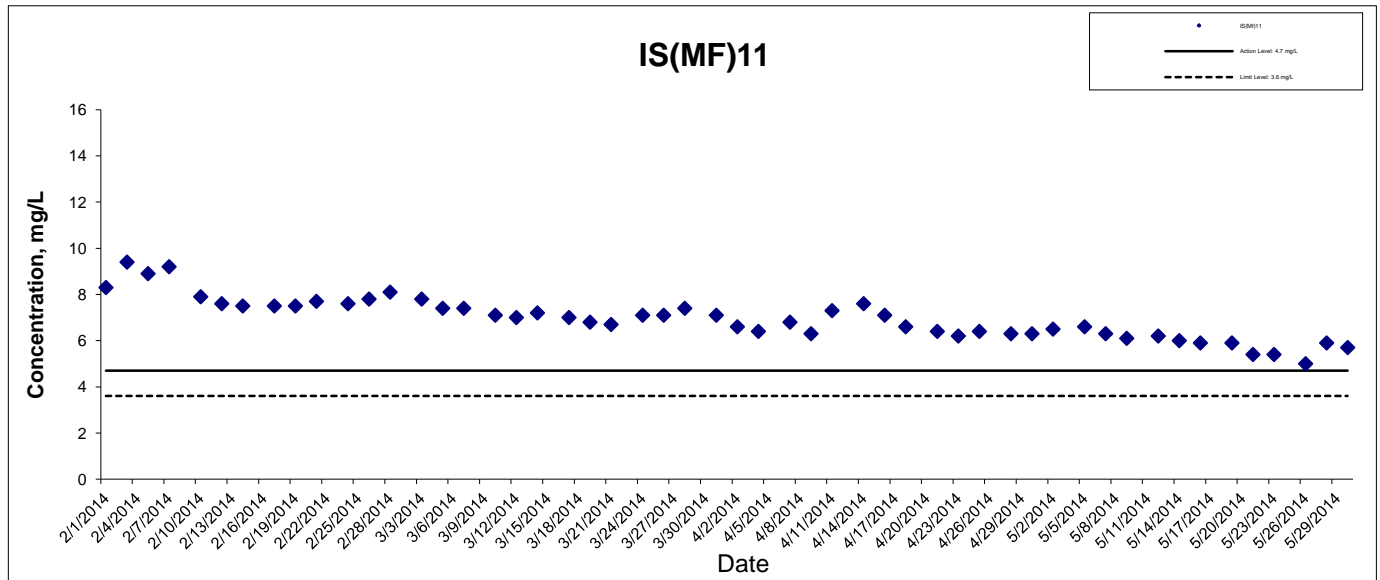




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Ebb Tide

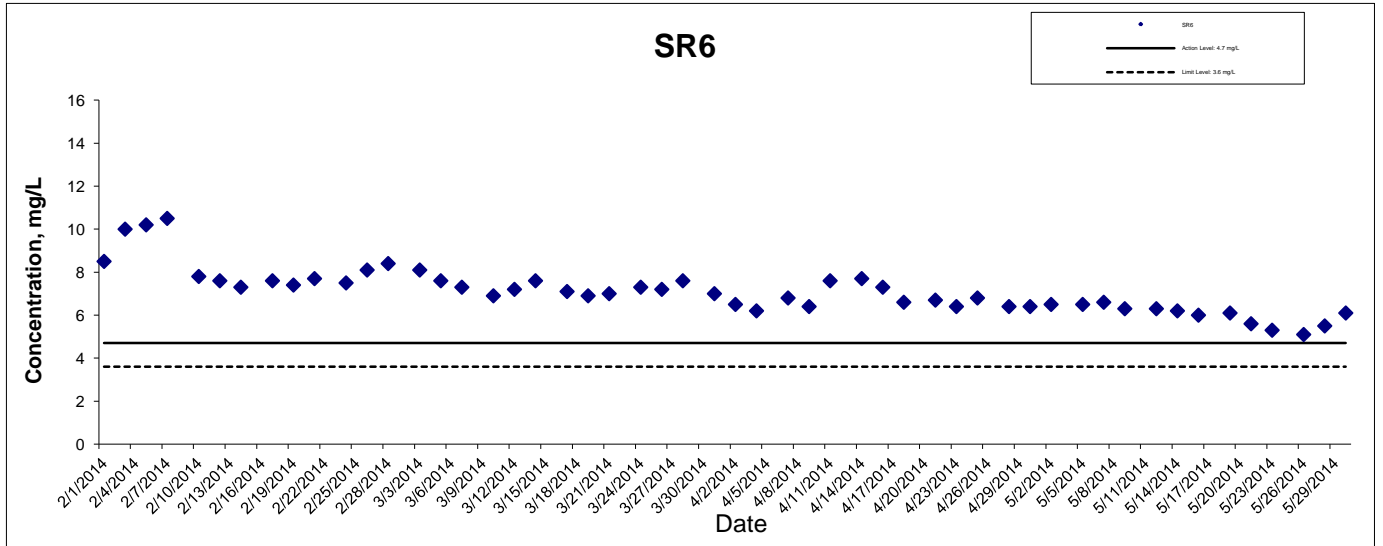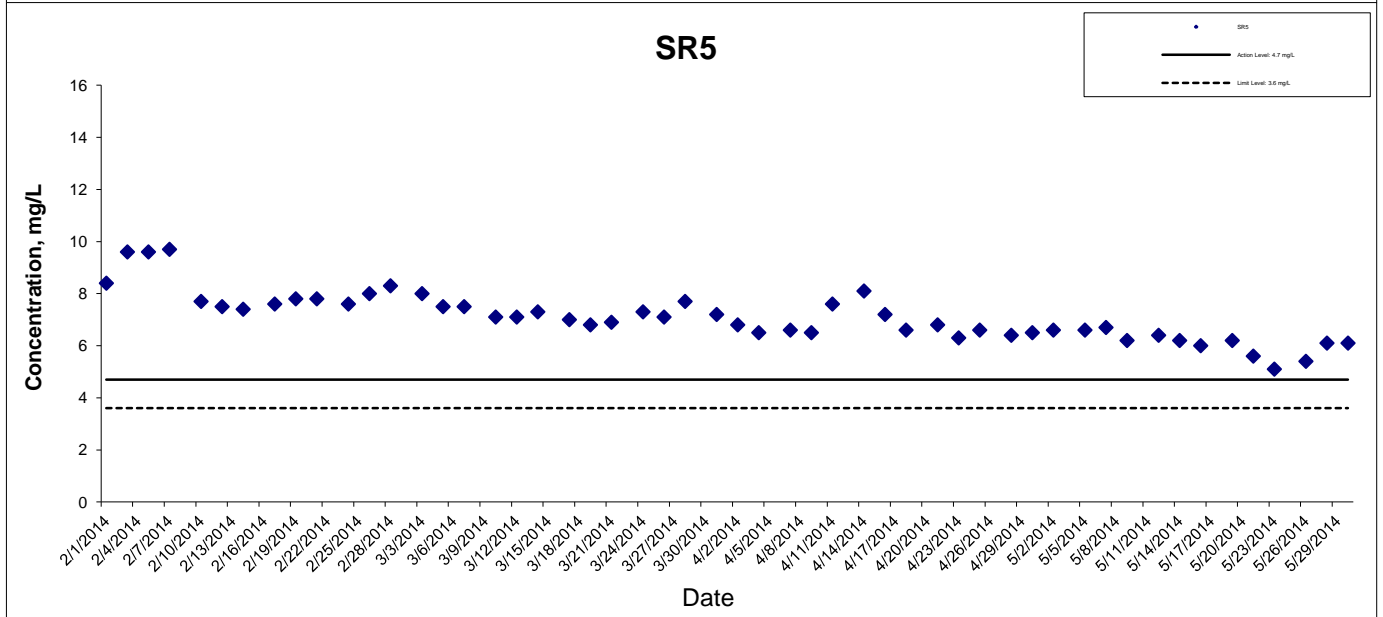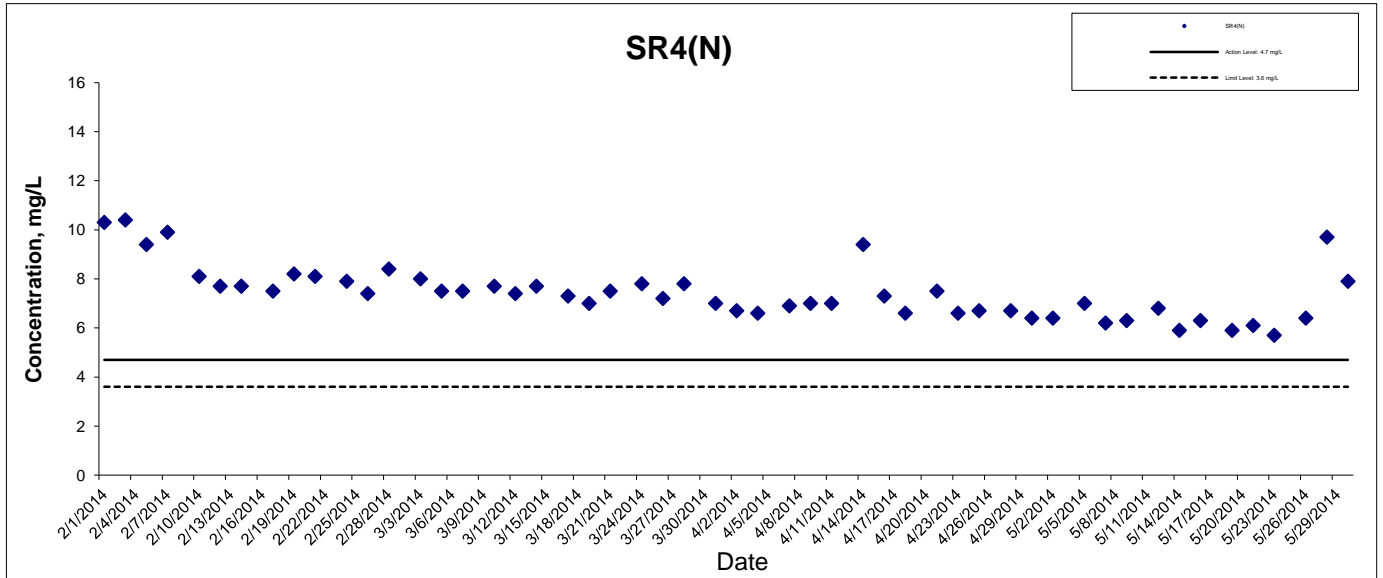


This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Ebb Tide

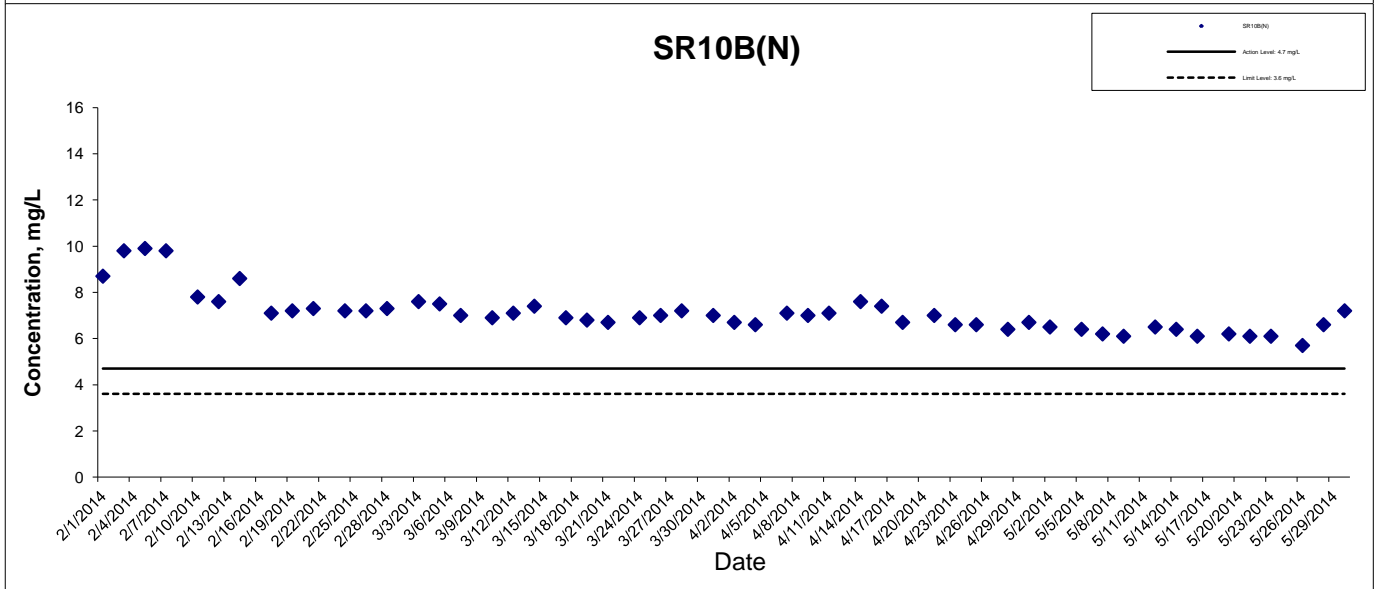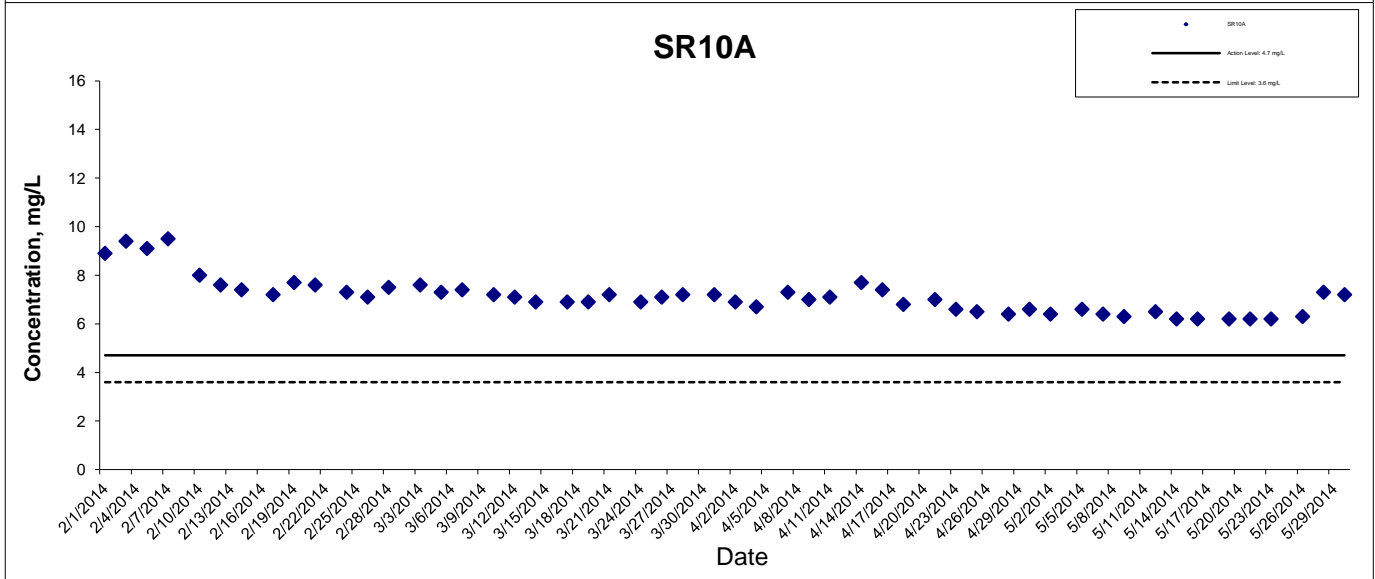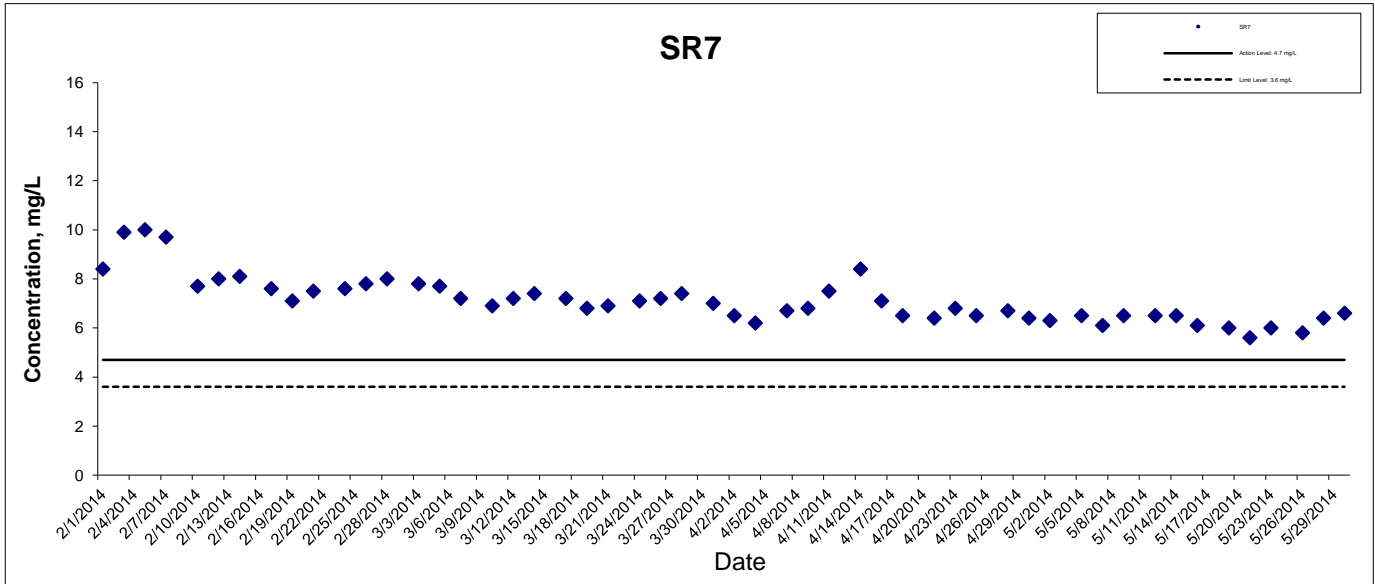


This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Flood Tide

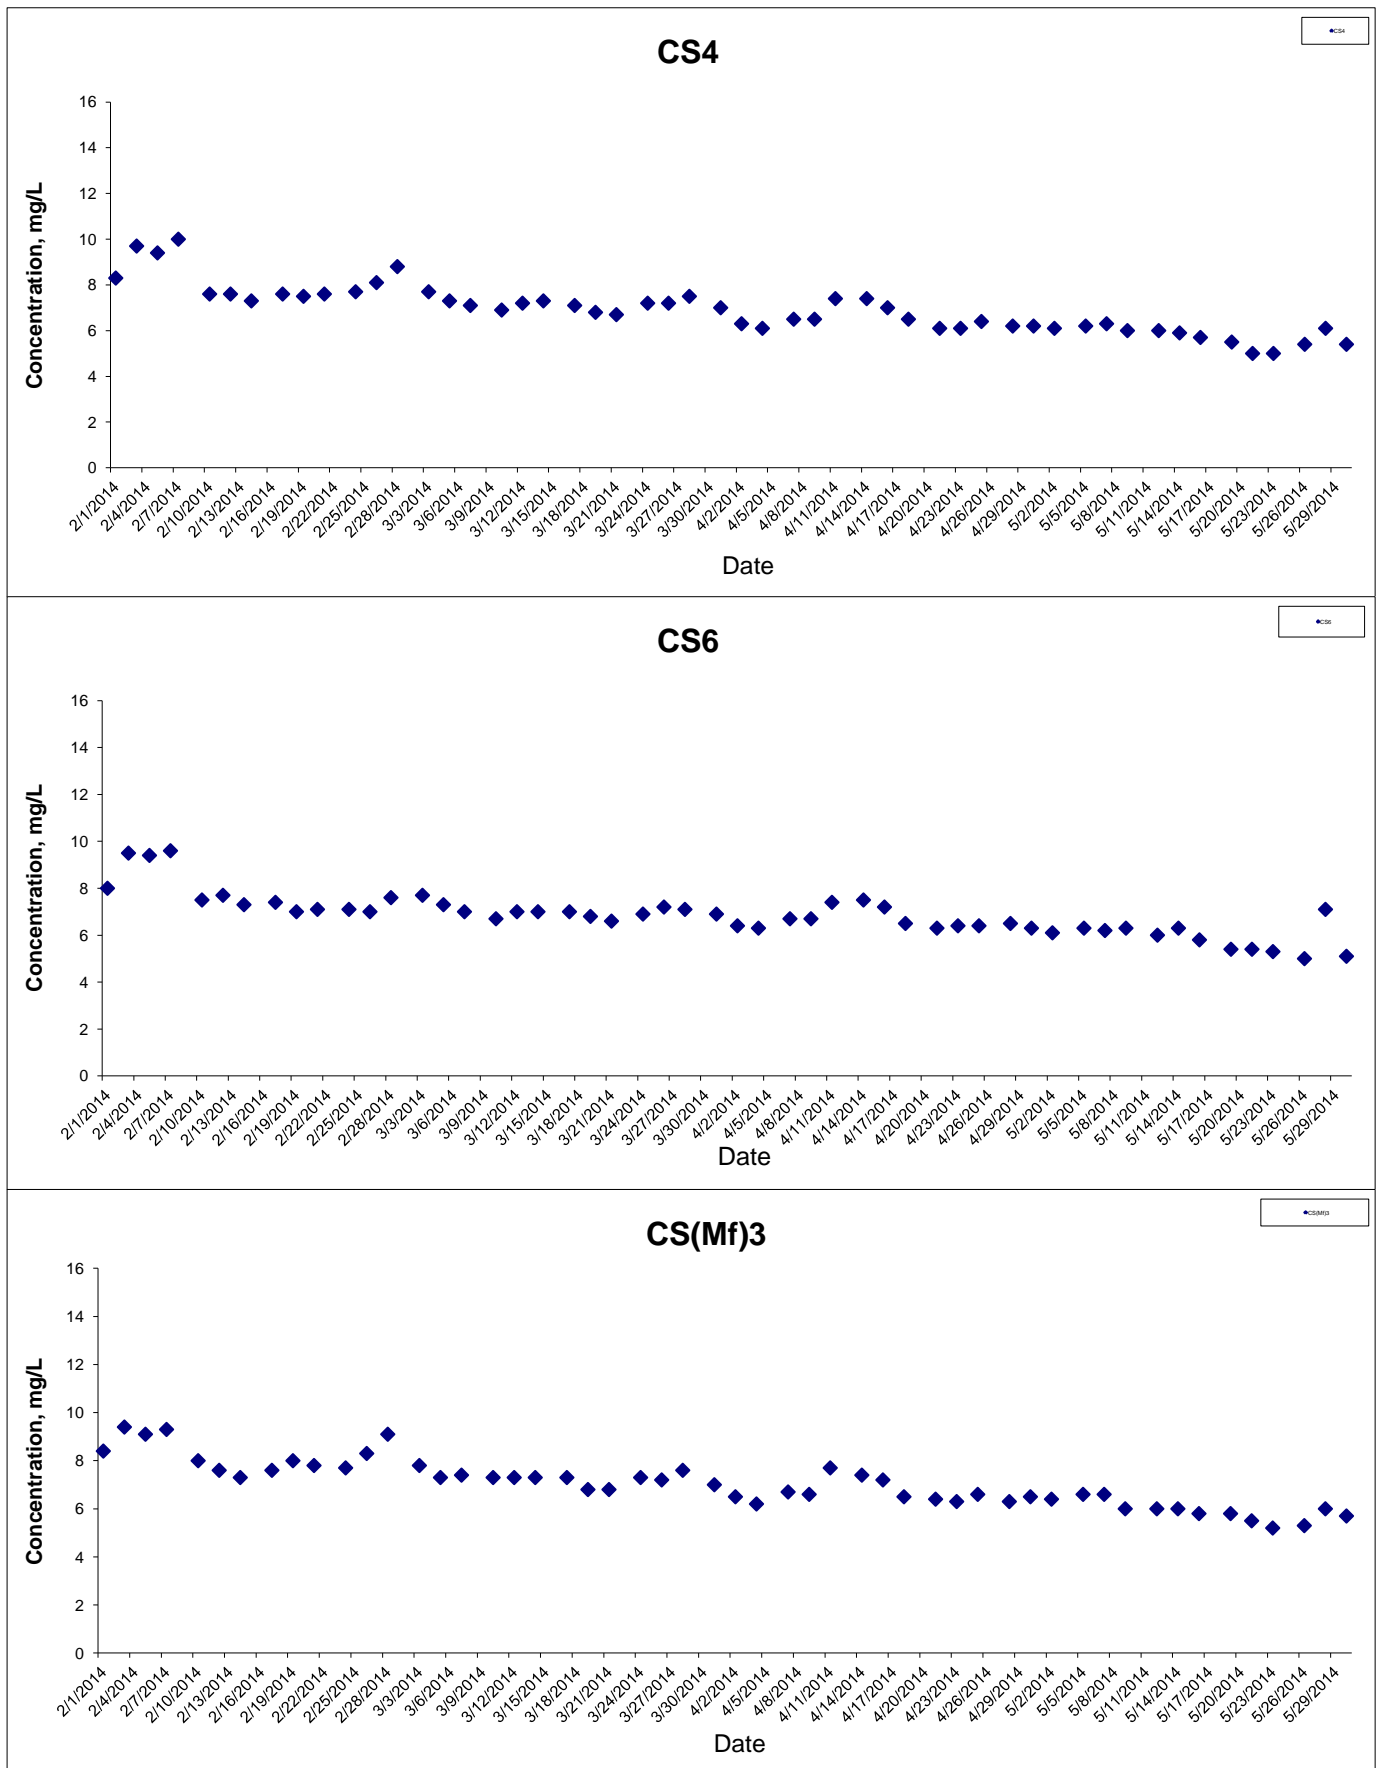




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Flood Tide

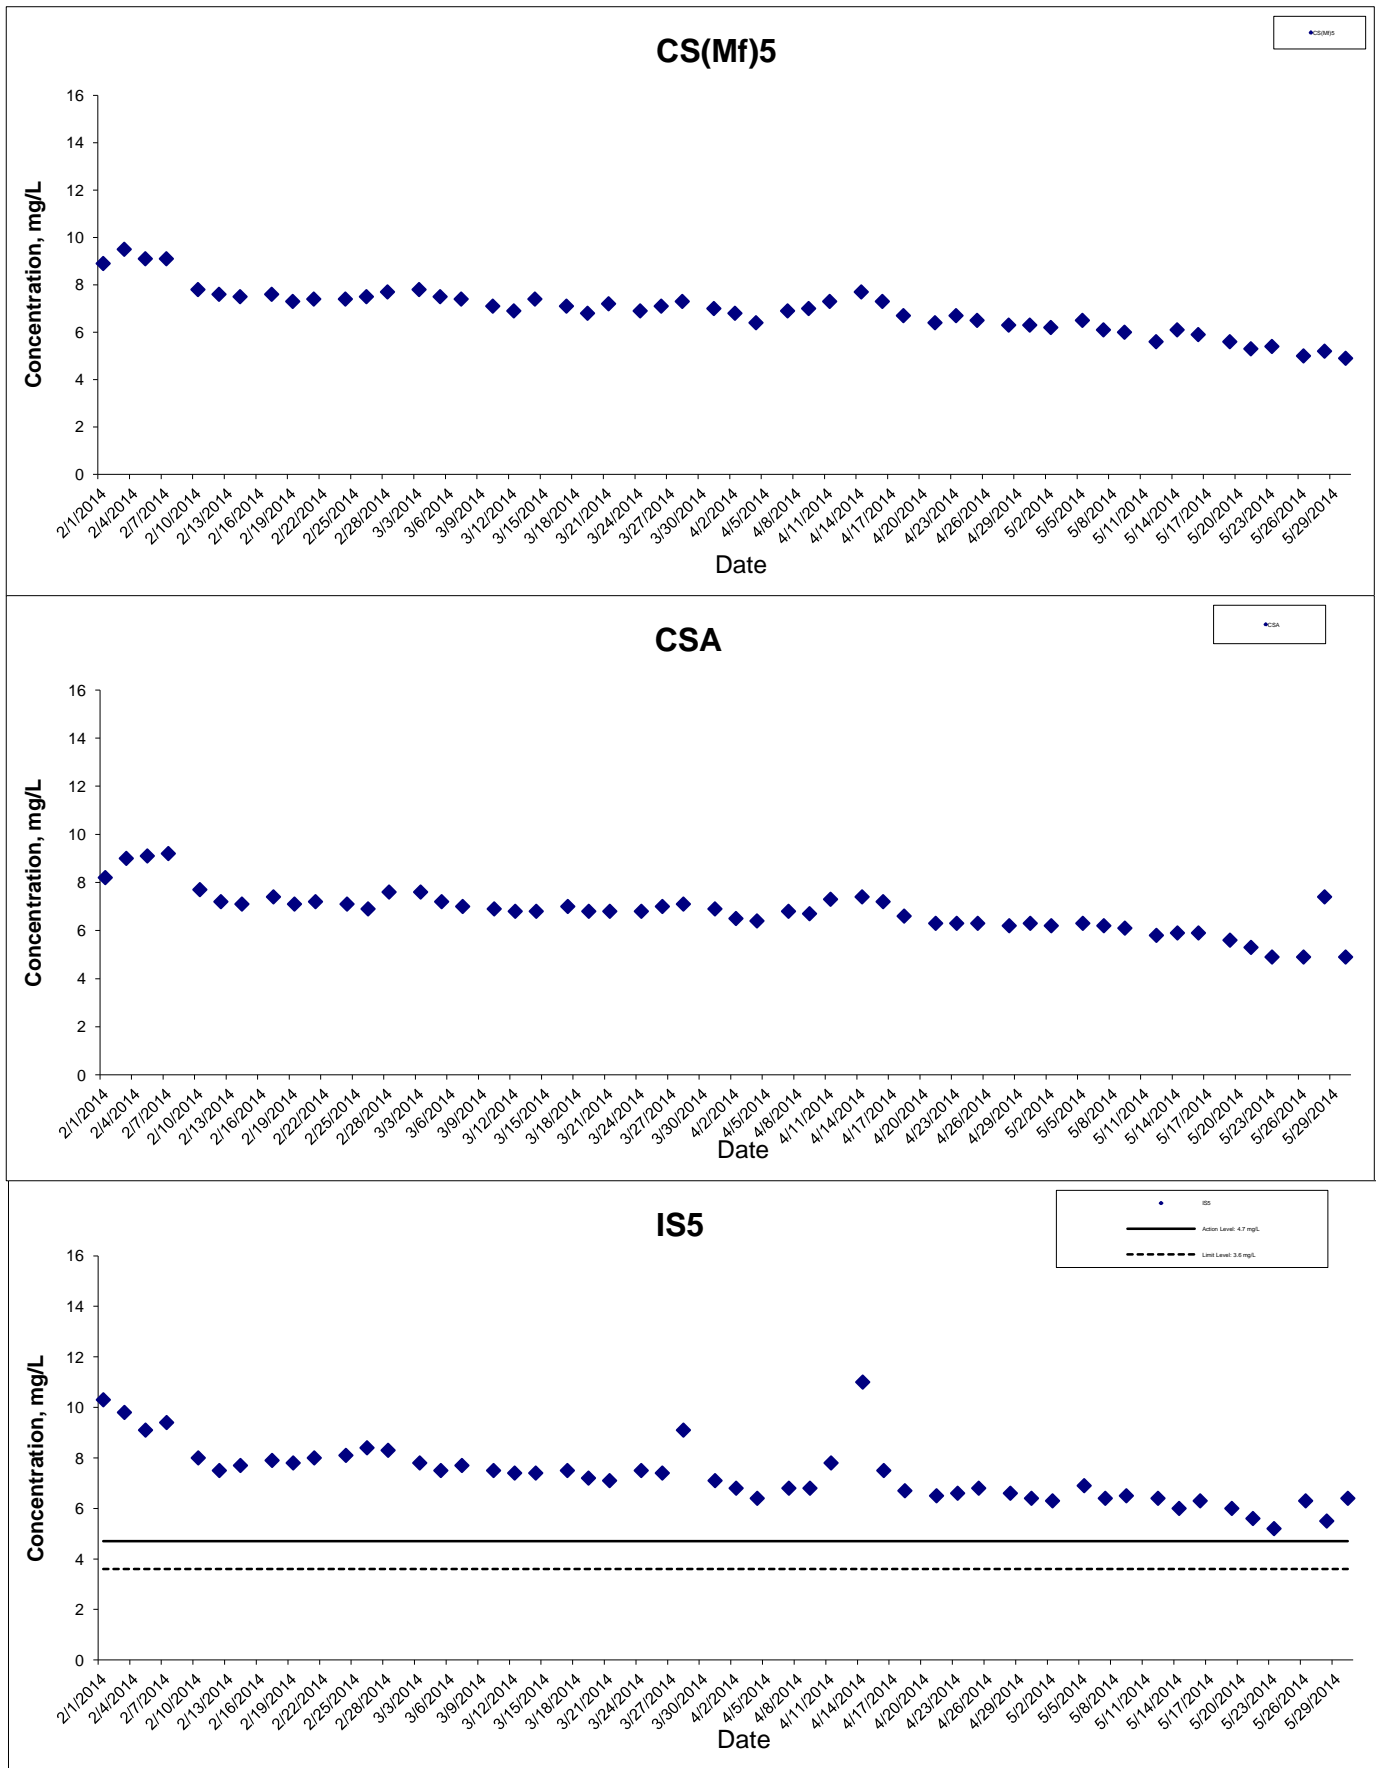


This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Flood Tide

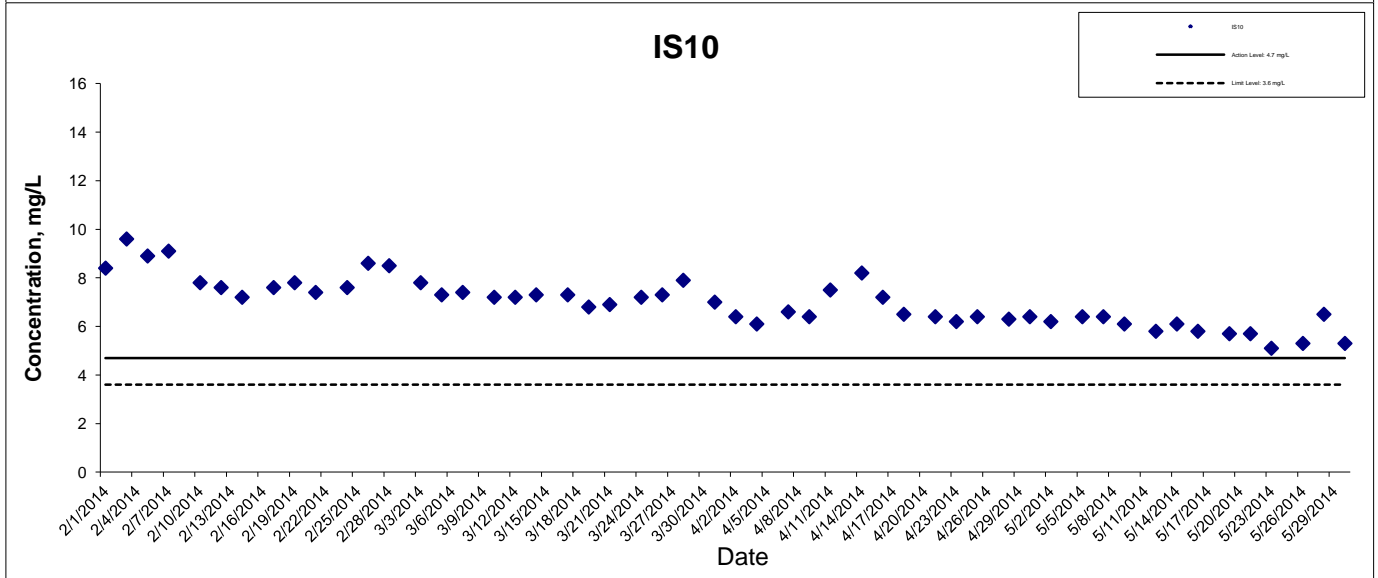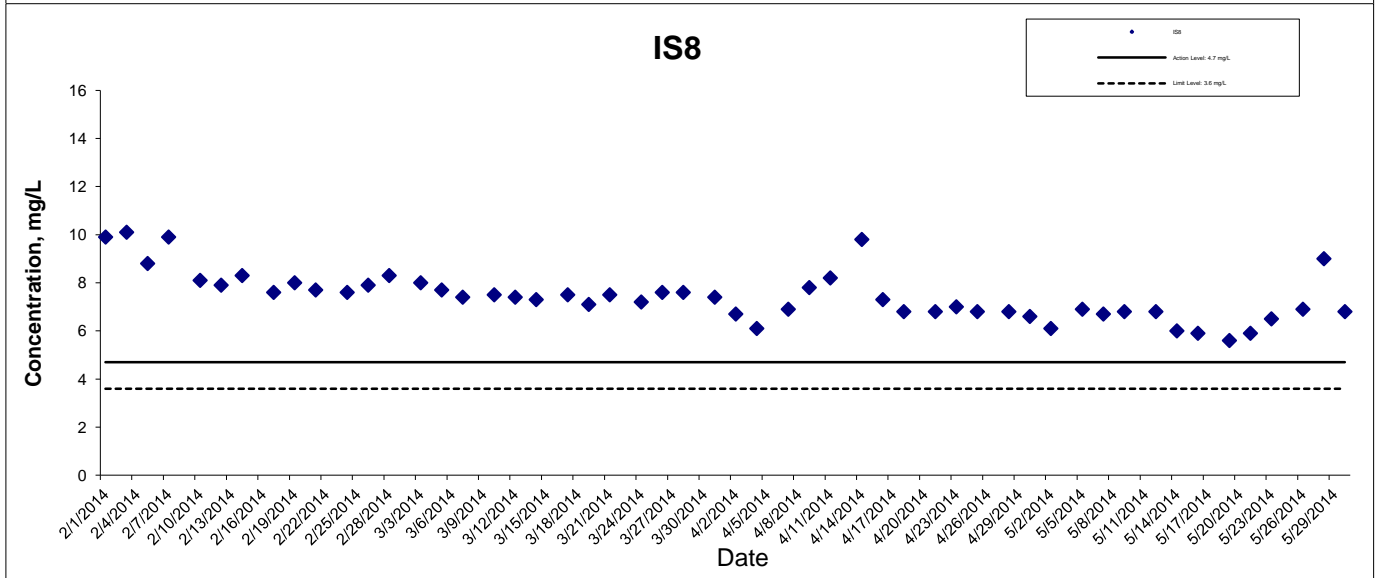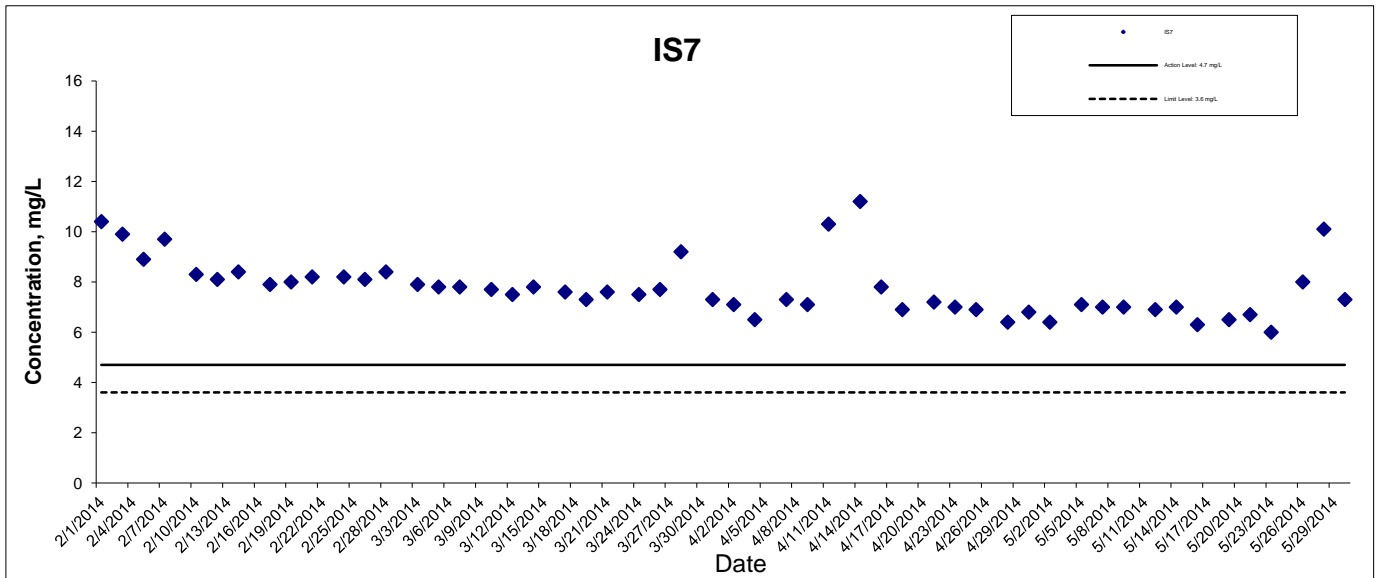




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Flood Tide

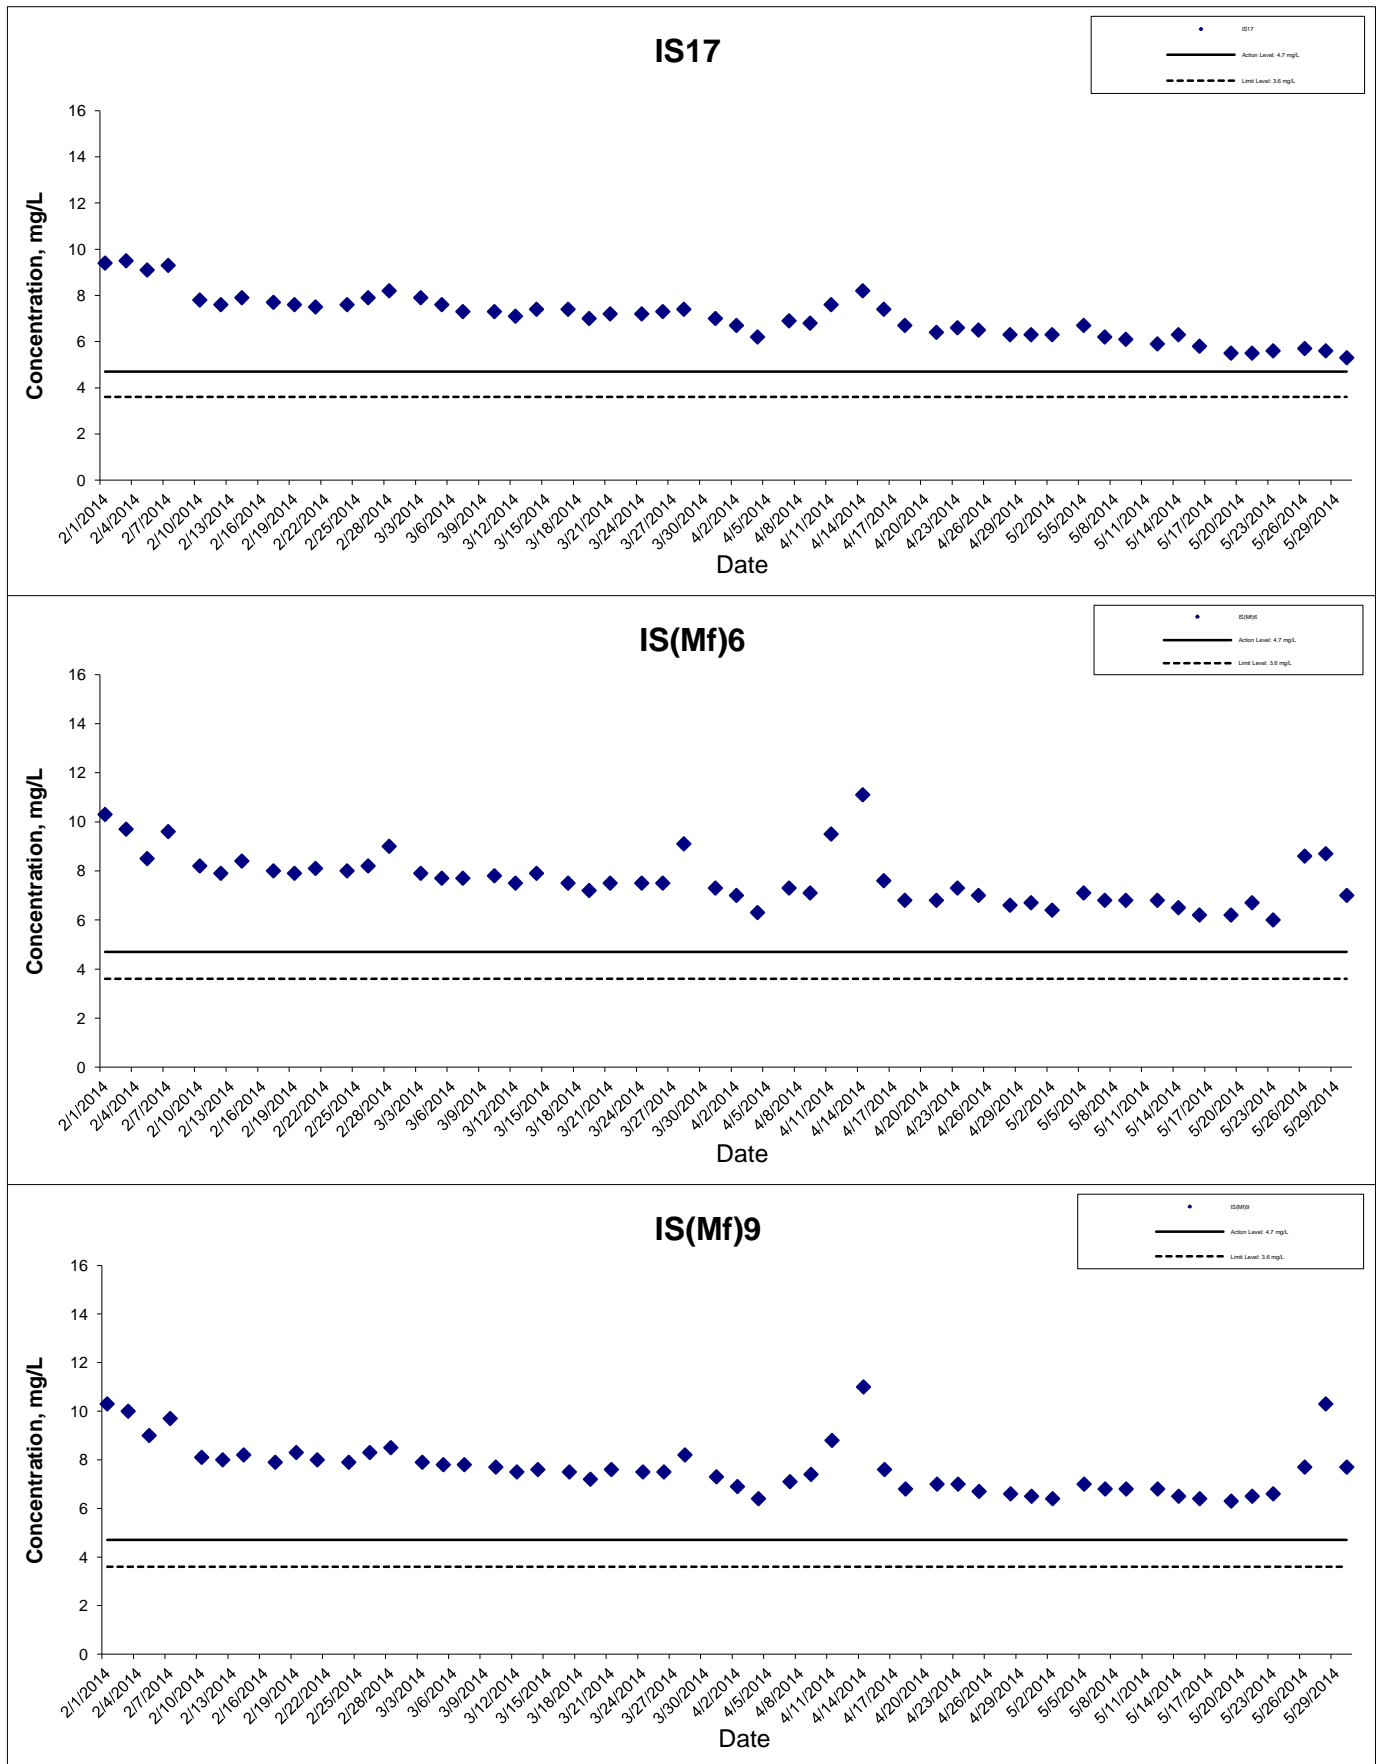

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.


Dissolved Oxygen (Bottom) at Mid-Flood Tide

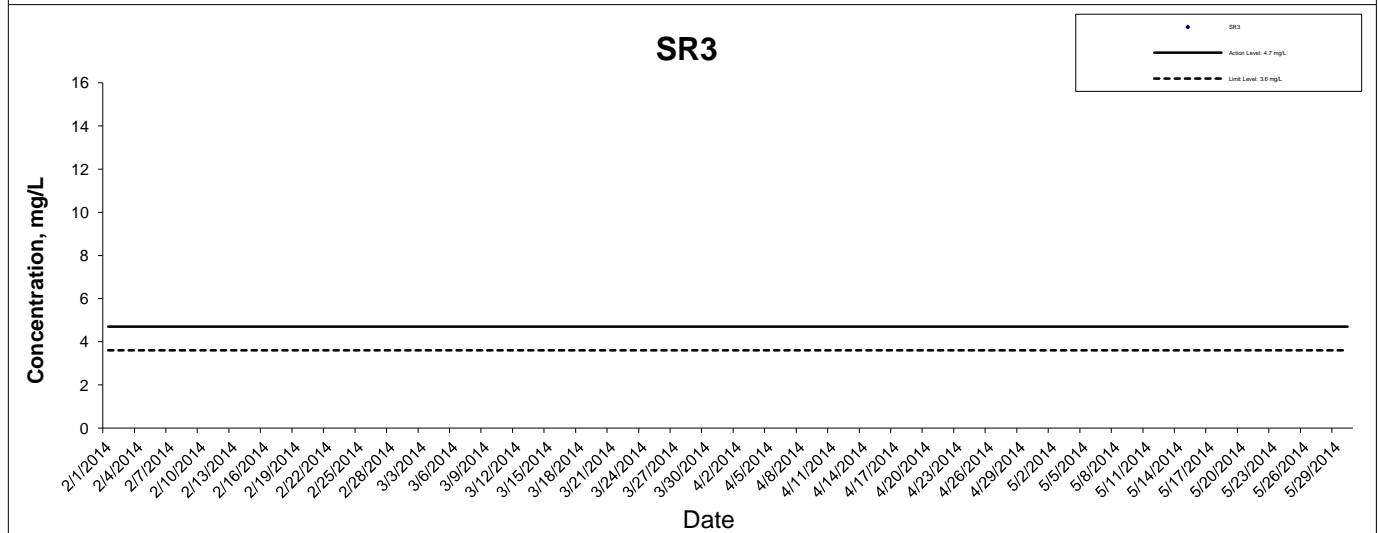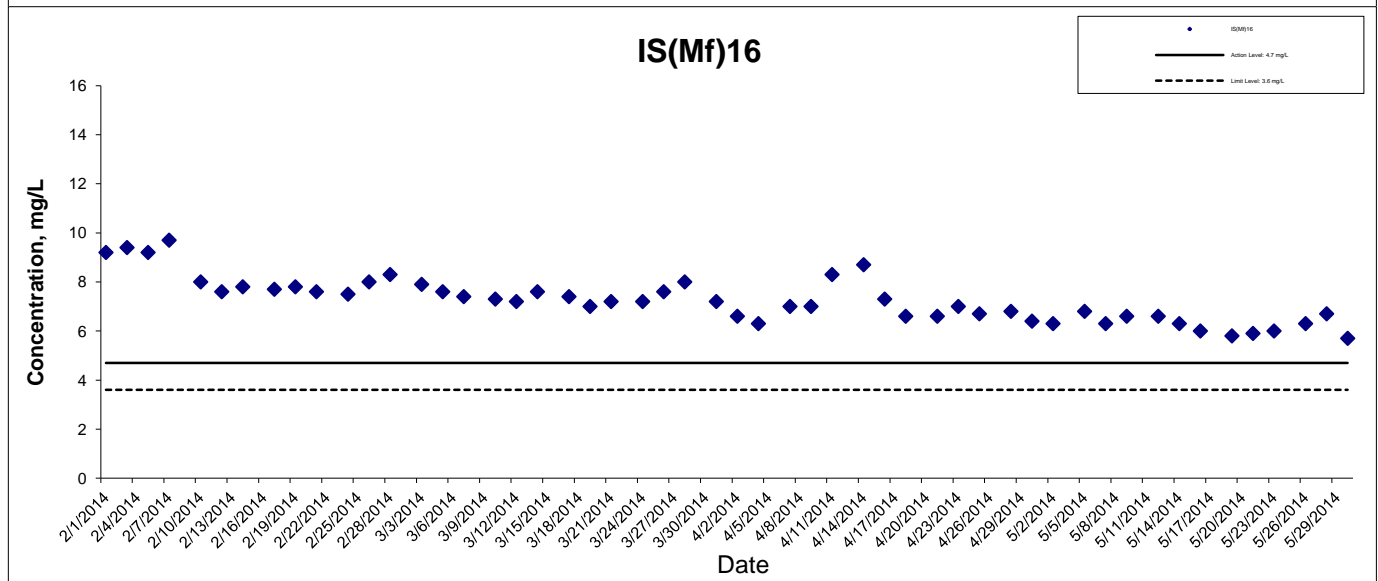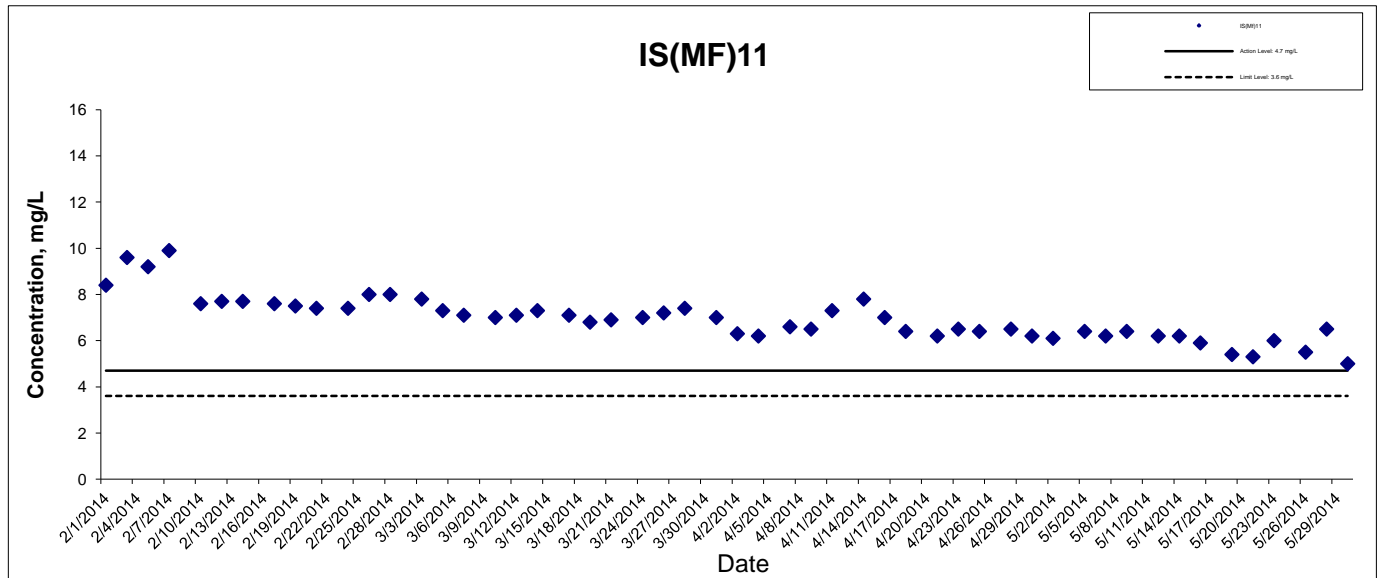

As the measured water depths were less than 3 m during all monitoring days, water samples are collected at mid-depth only.

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Bottom) at Mid-Flood Tide

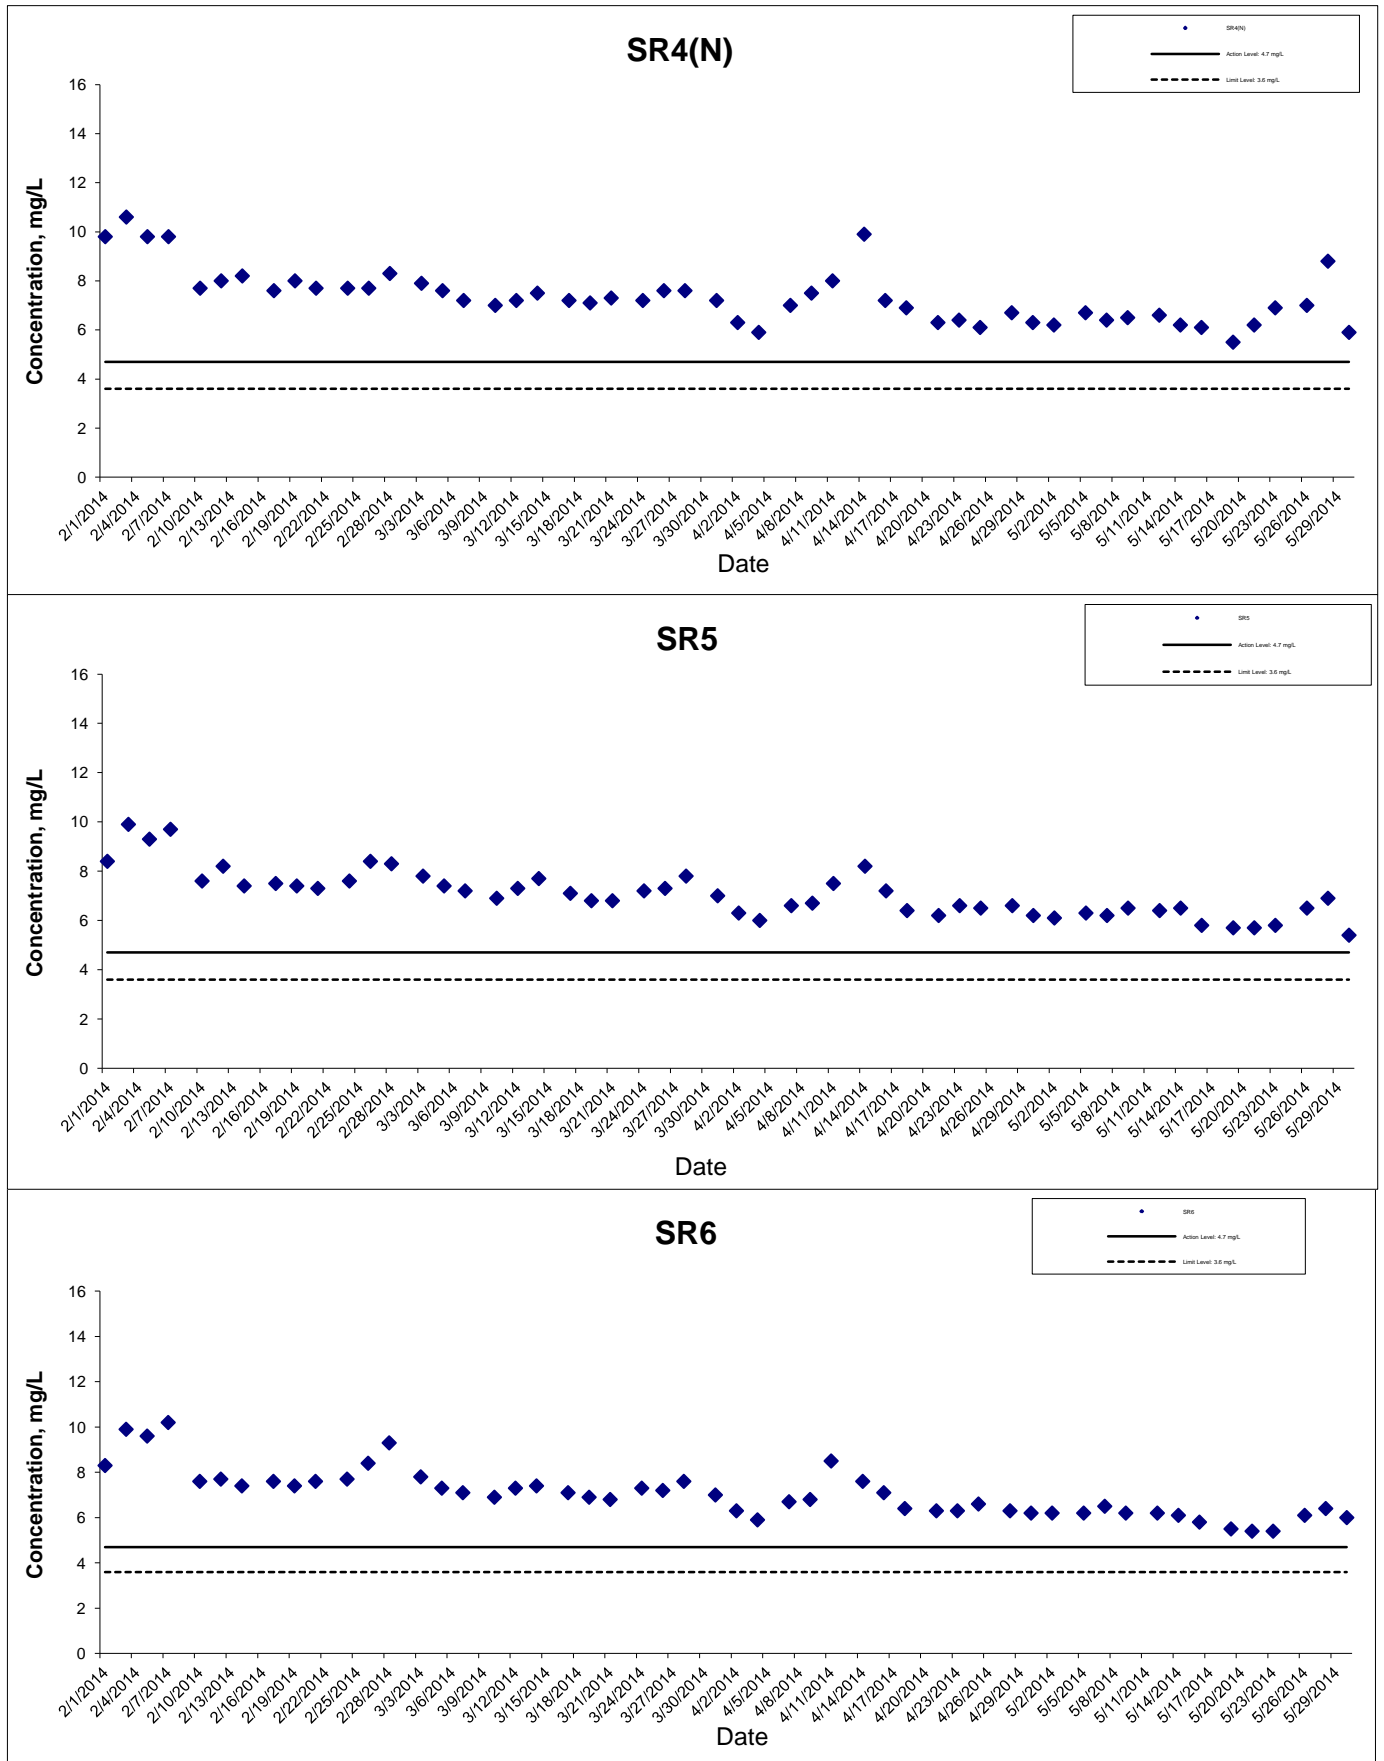




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
 HONG KONG BOUNDARY CROSSING FACILITIES
 - RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
 Monitoring Results






Dissolved Oxygen (Bottom) at Mid-Flood Tide

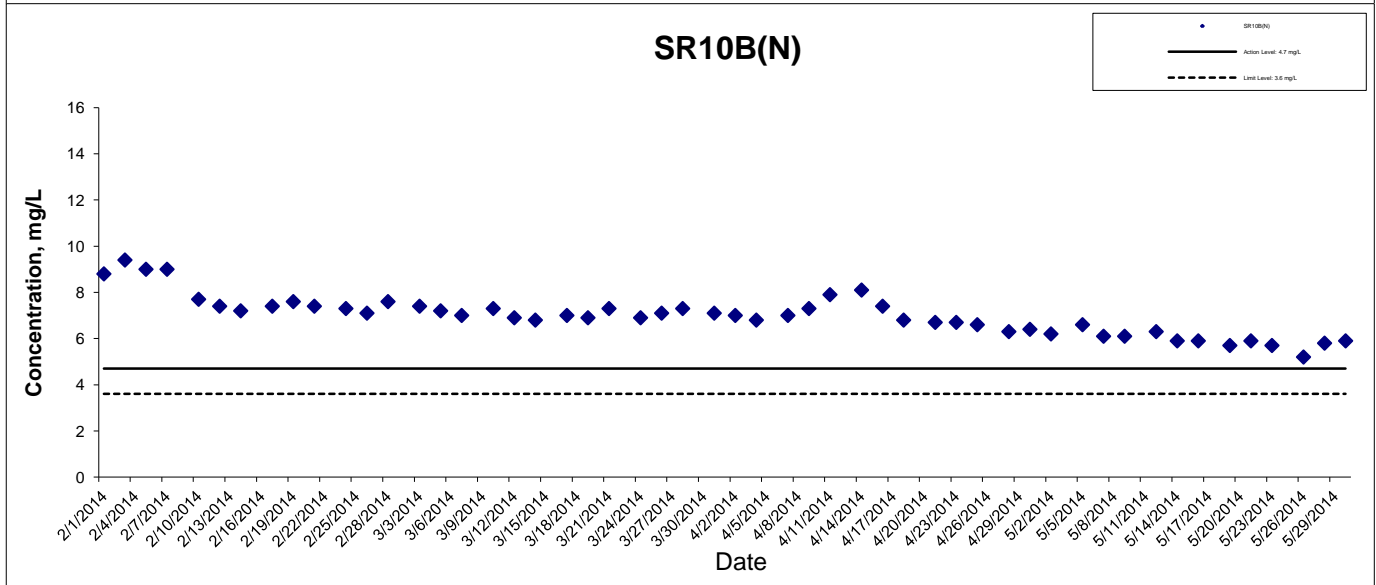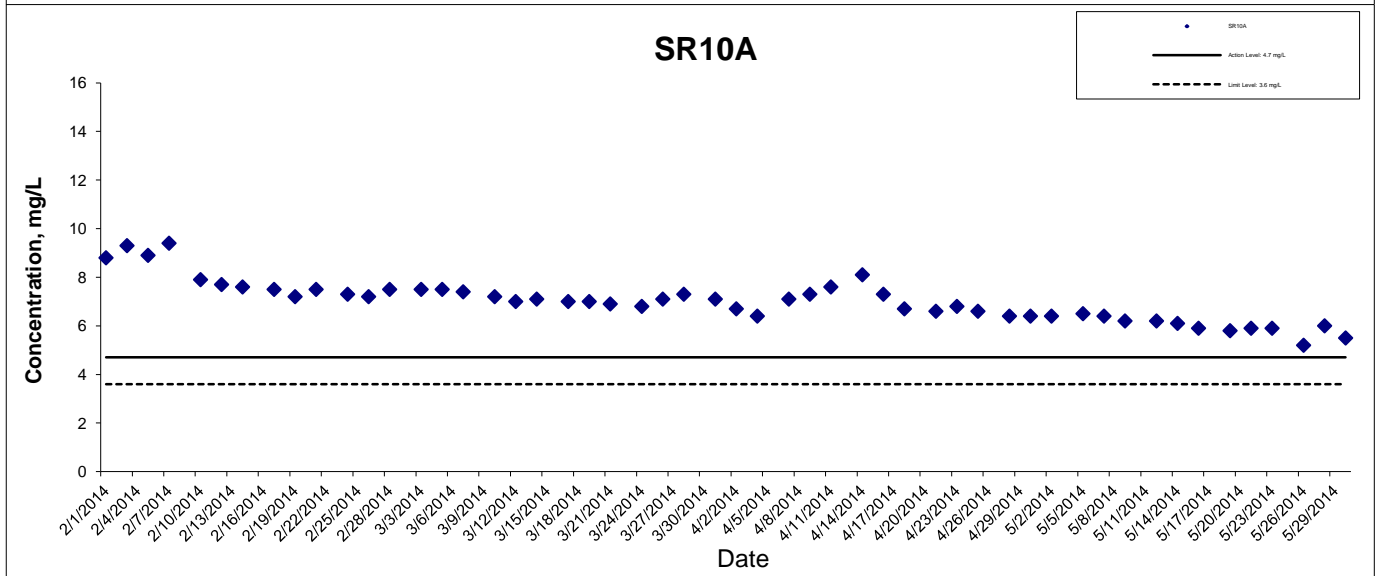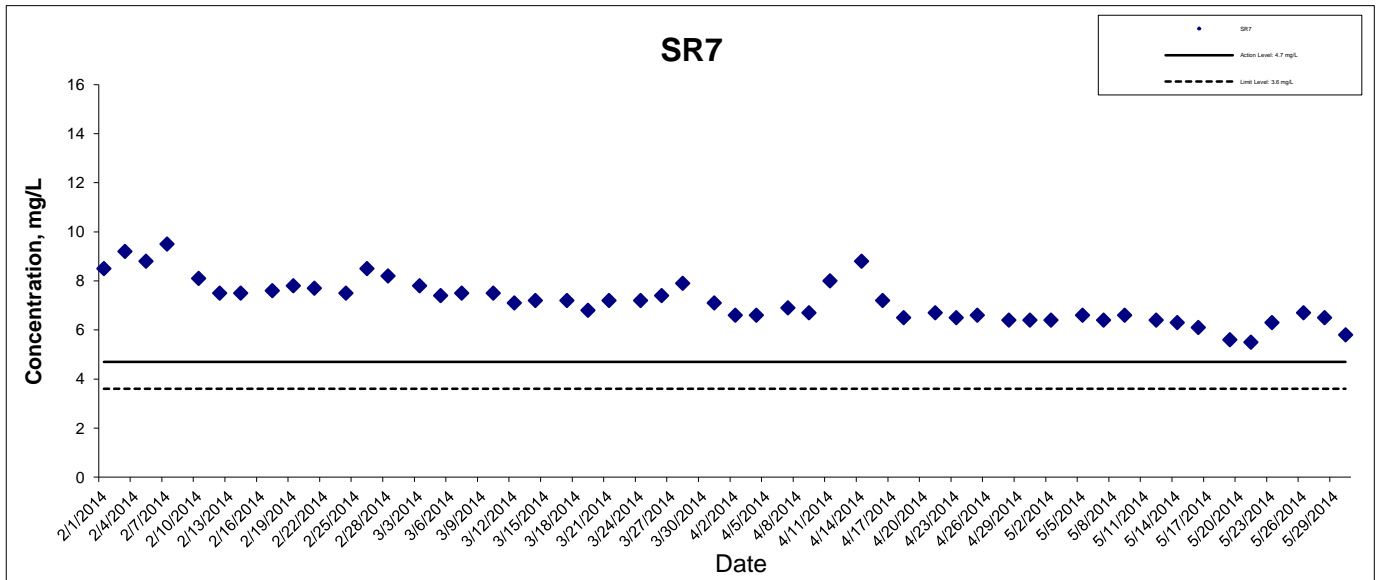




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

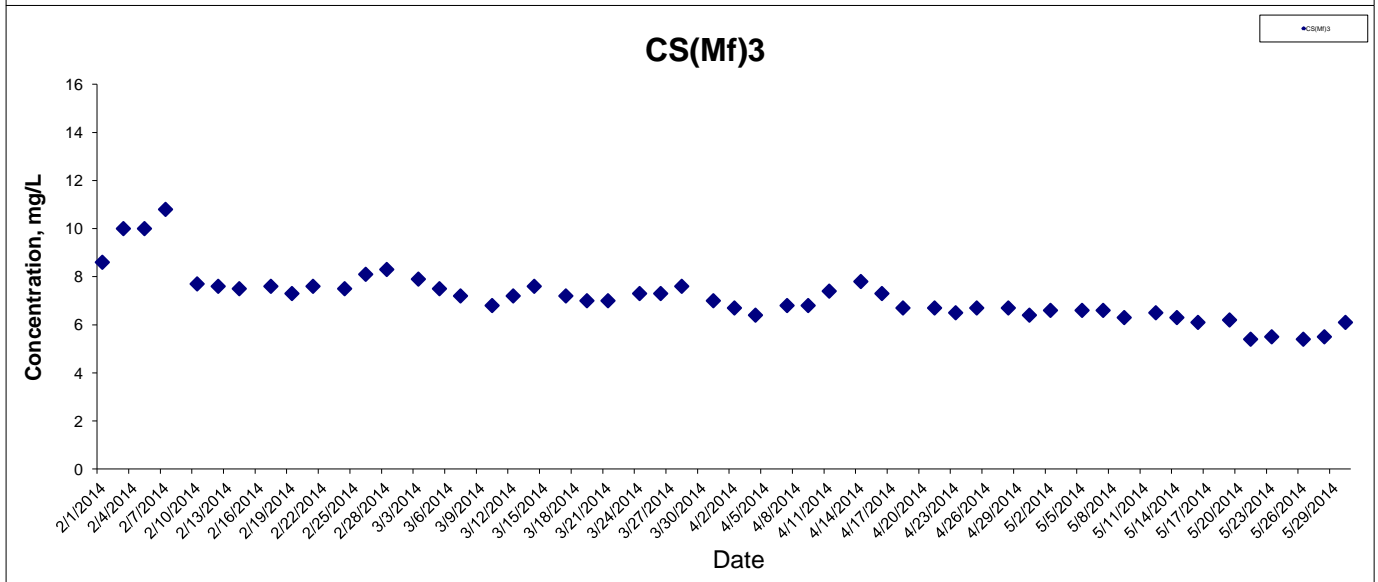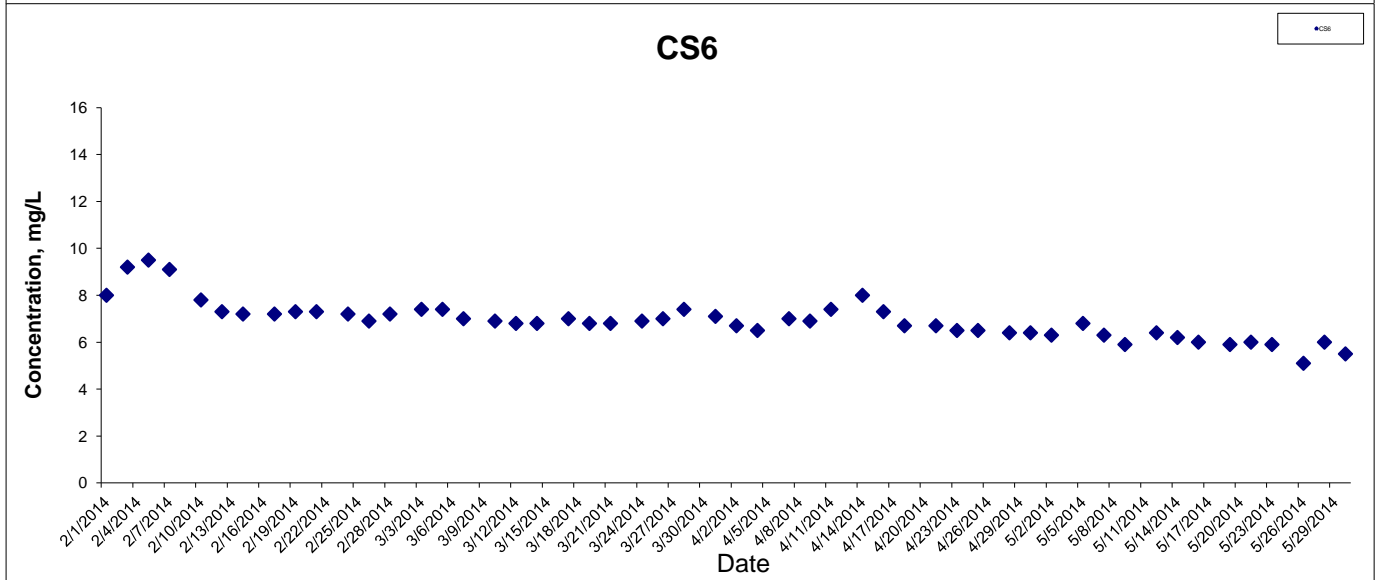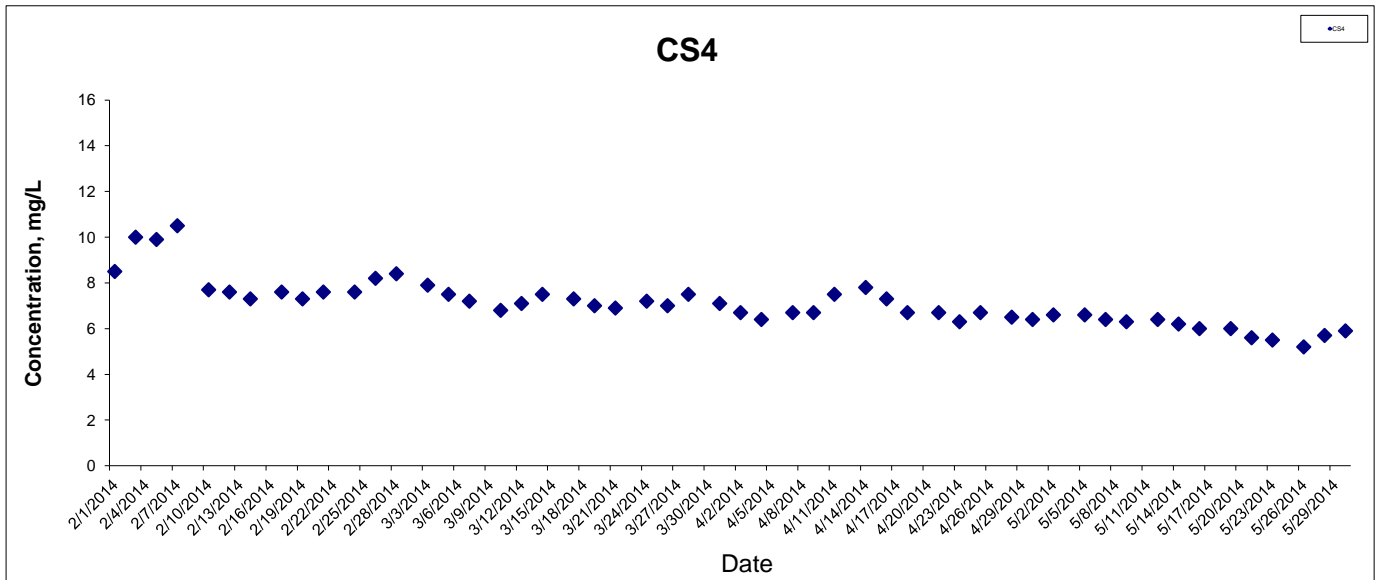




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

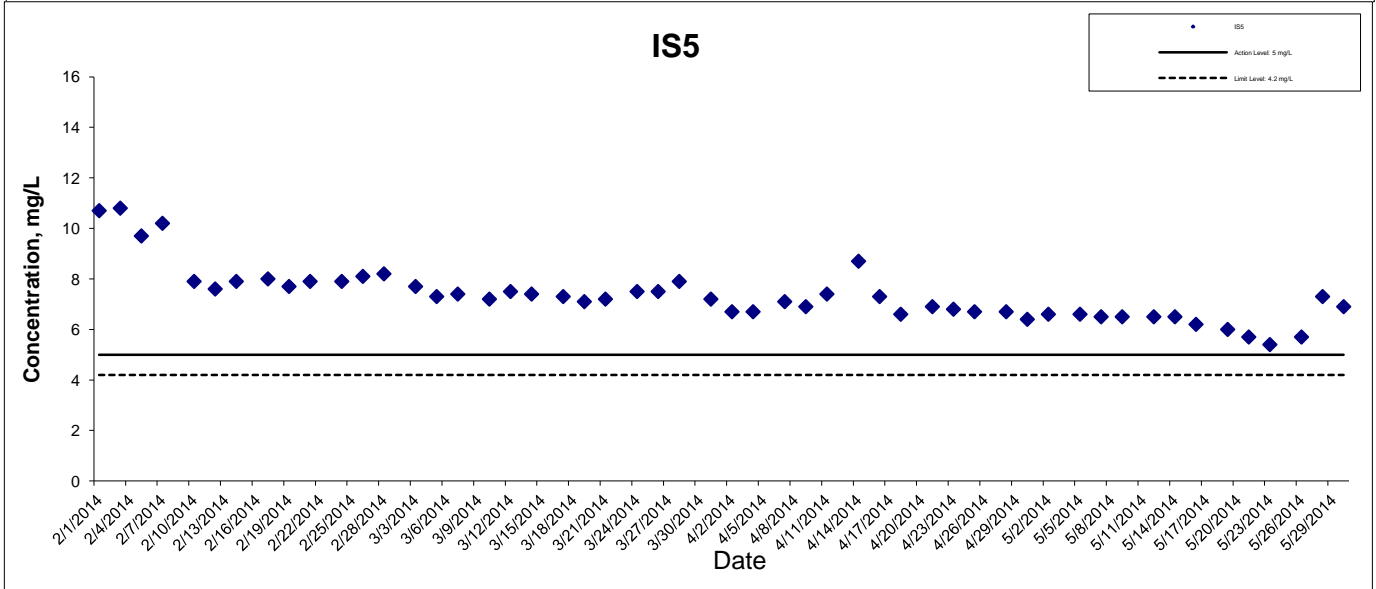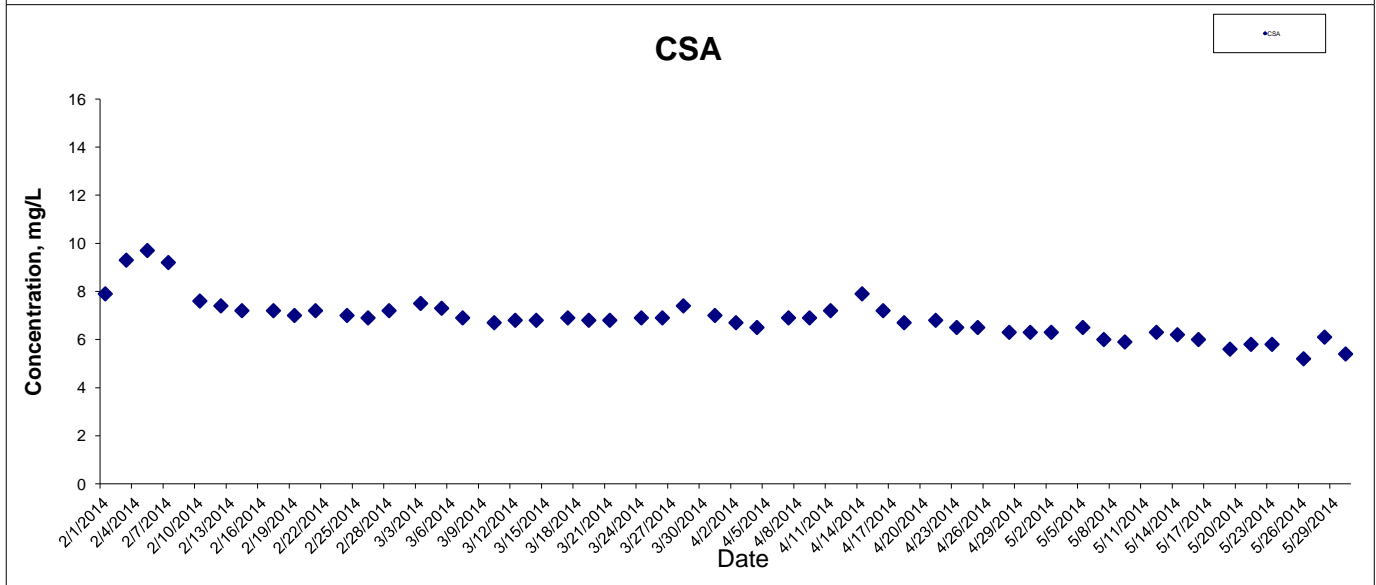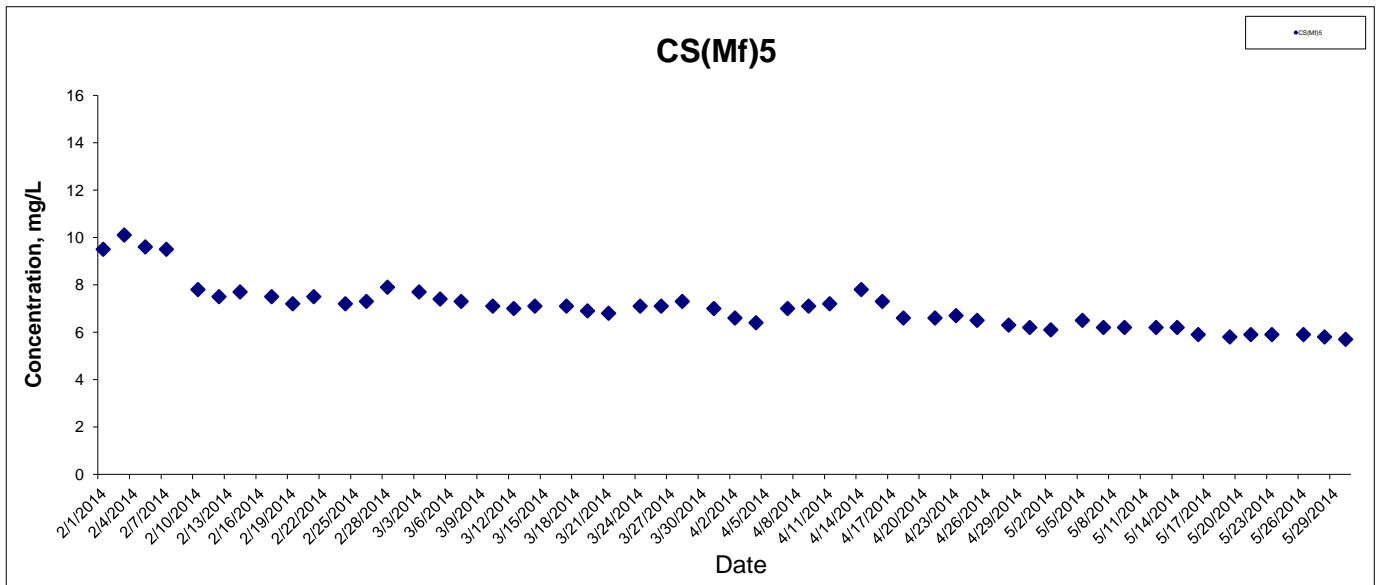


This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

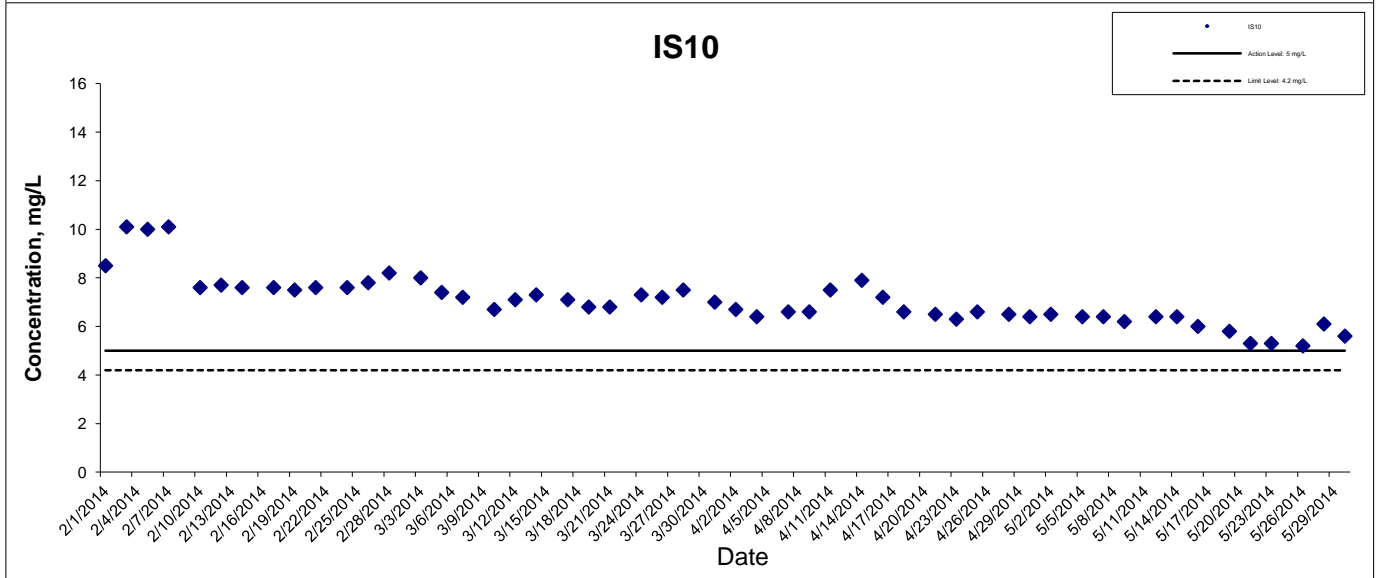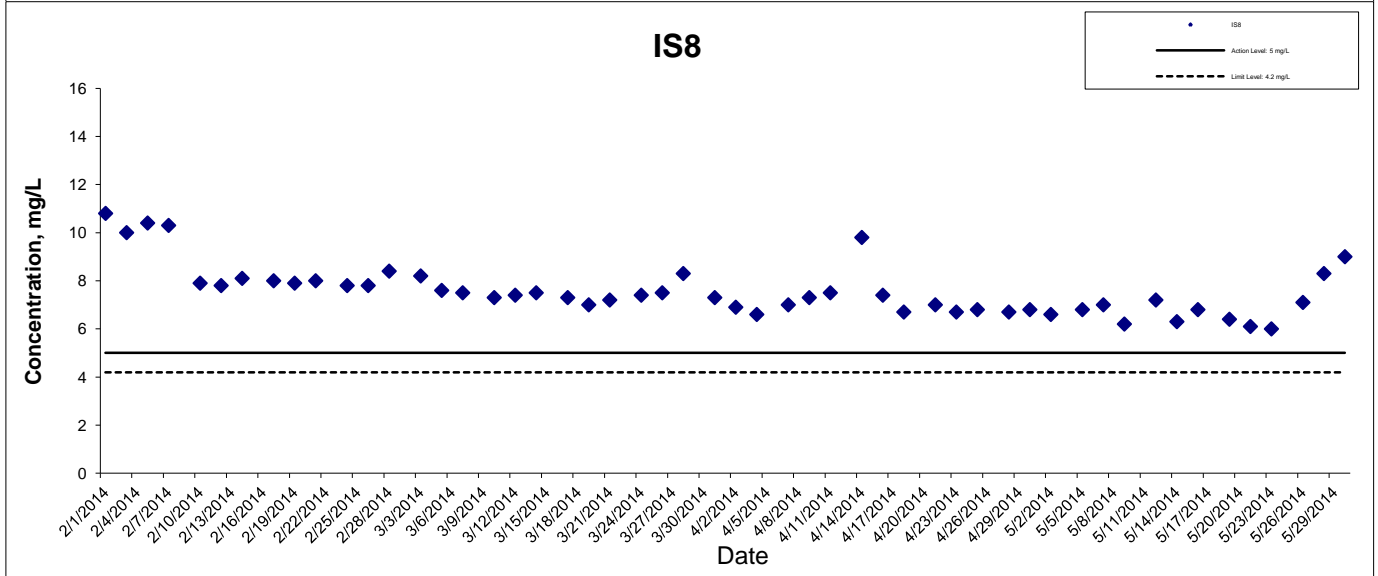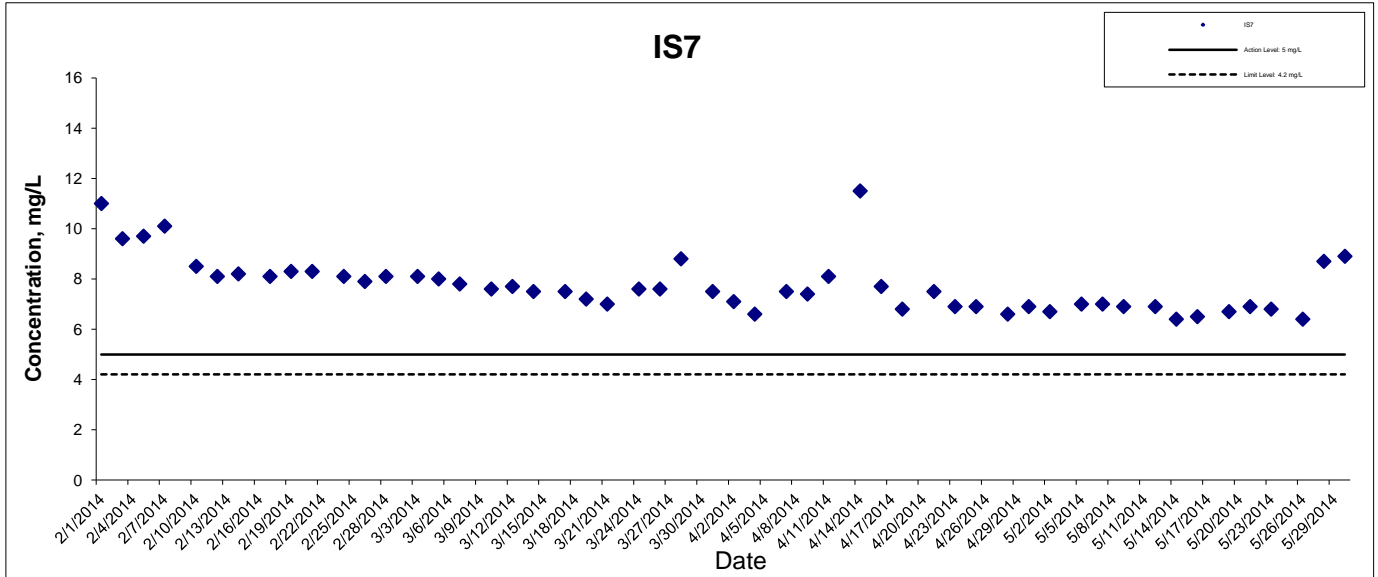

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.




Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

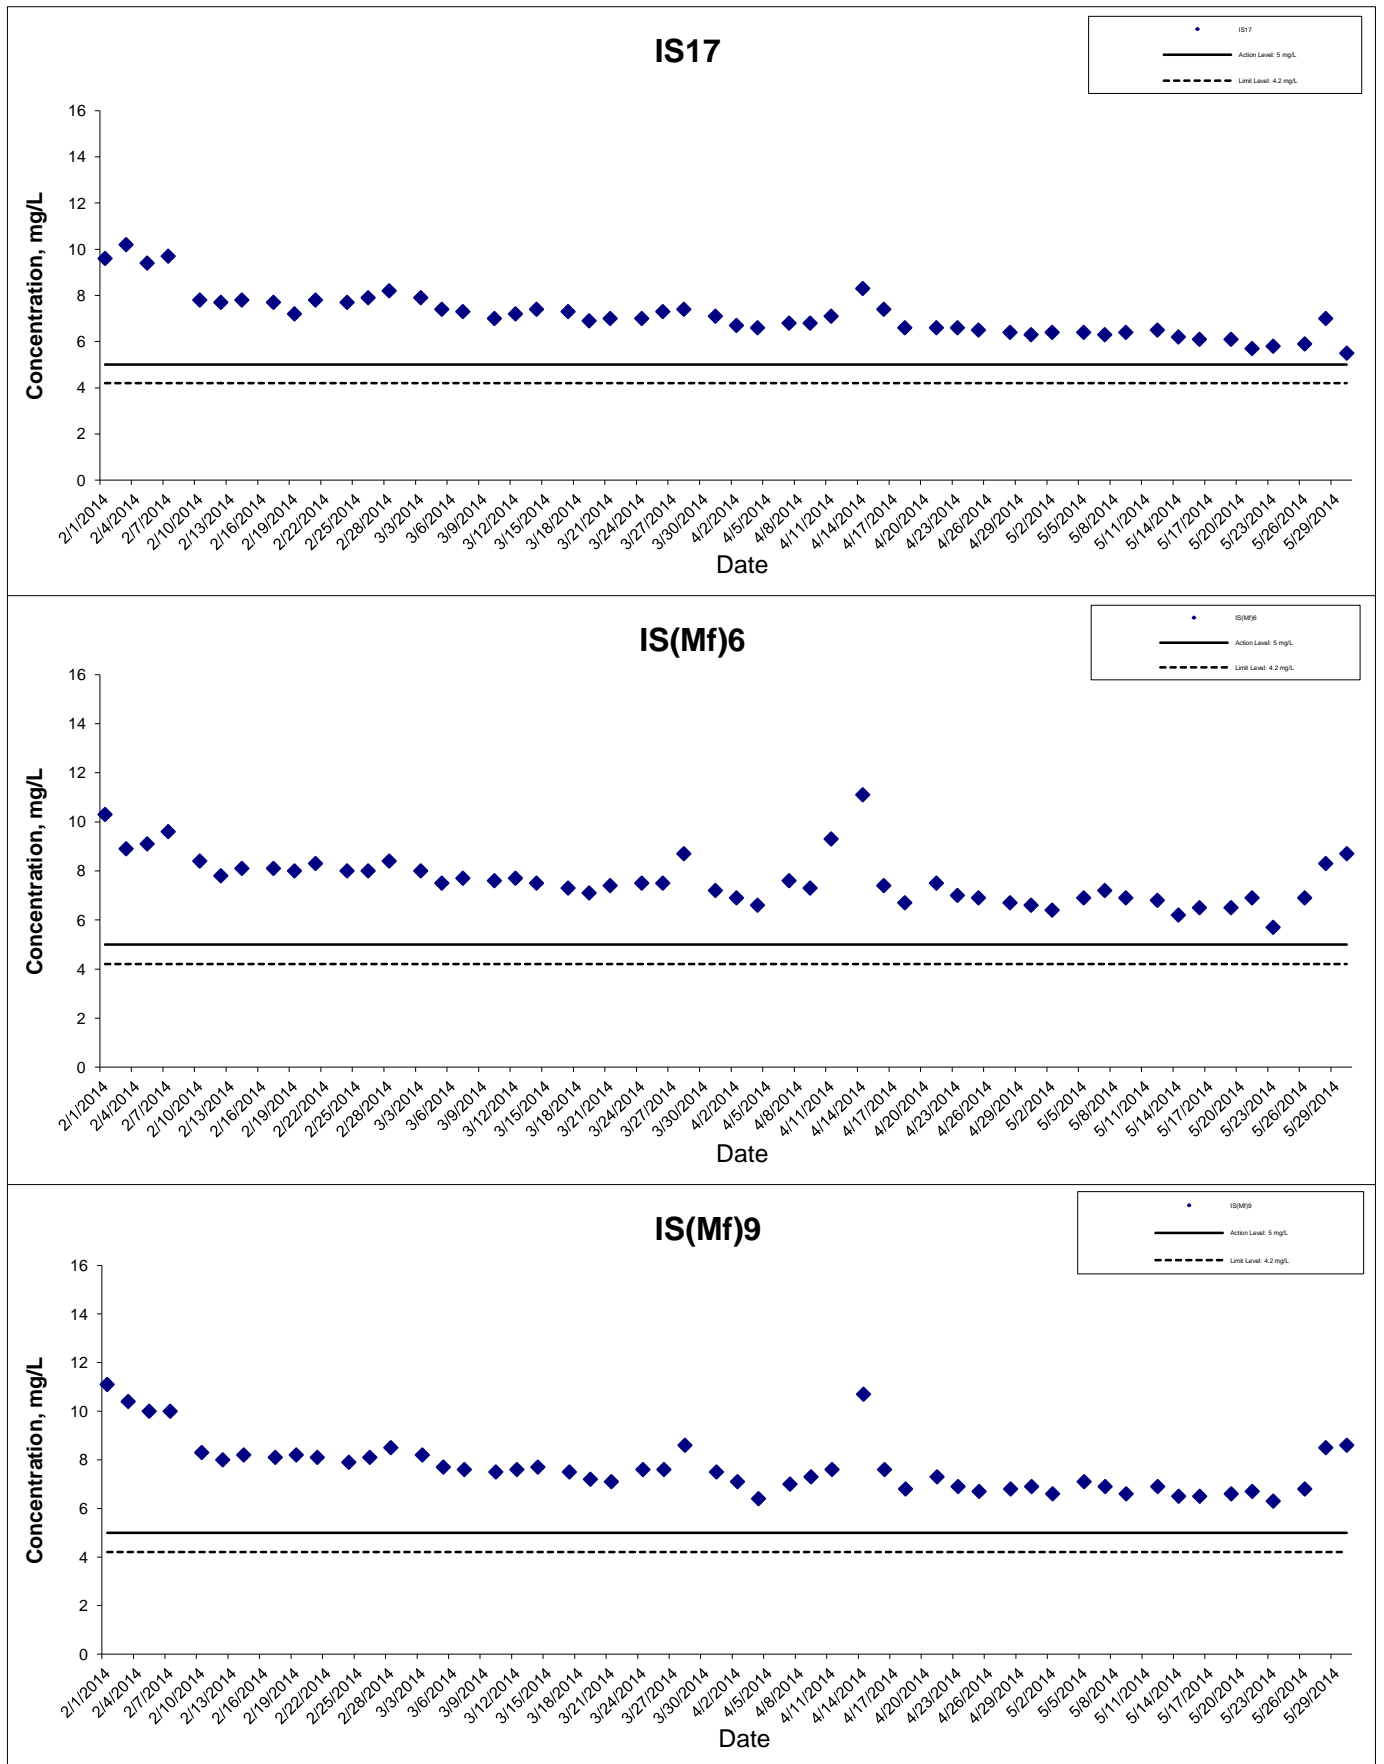

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.






Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

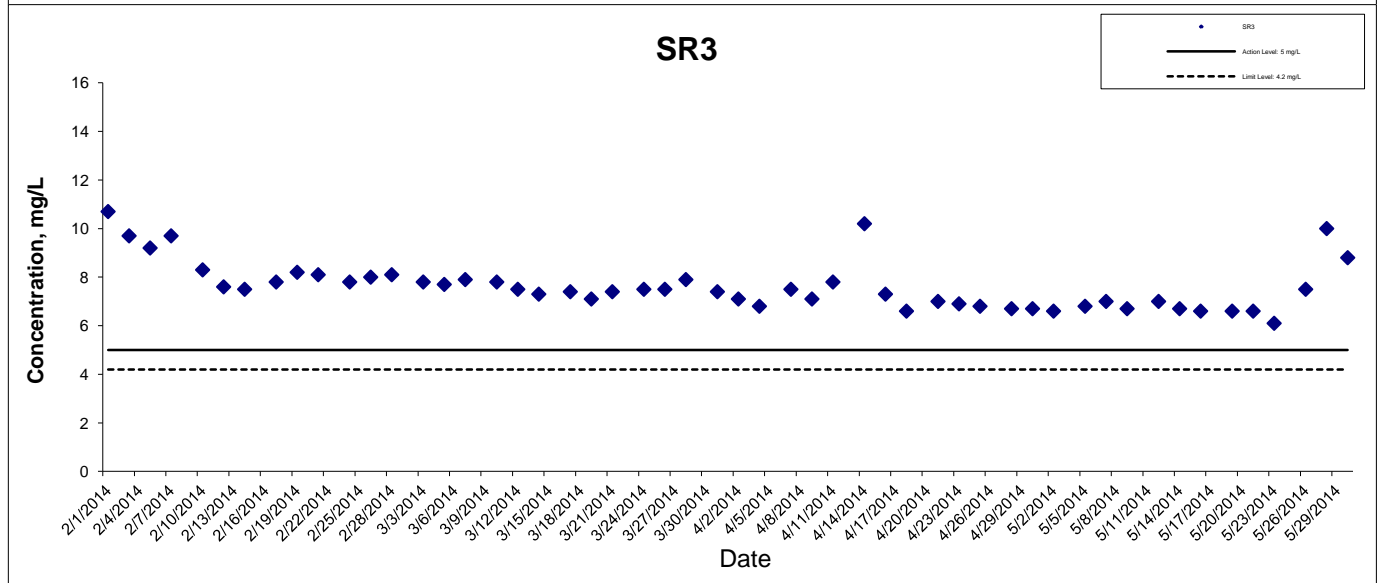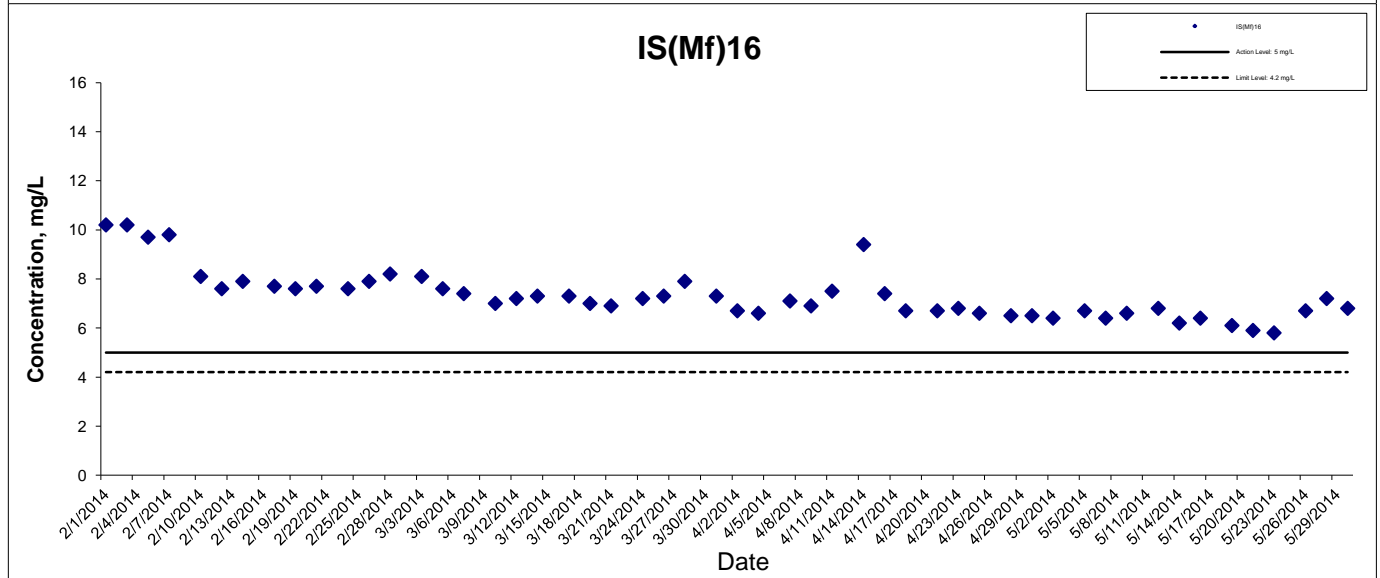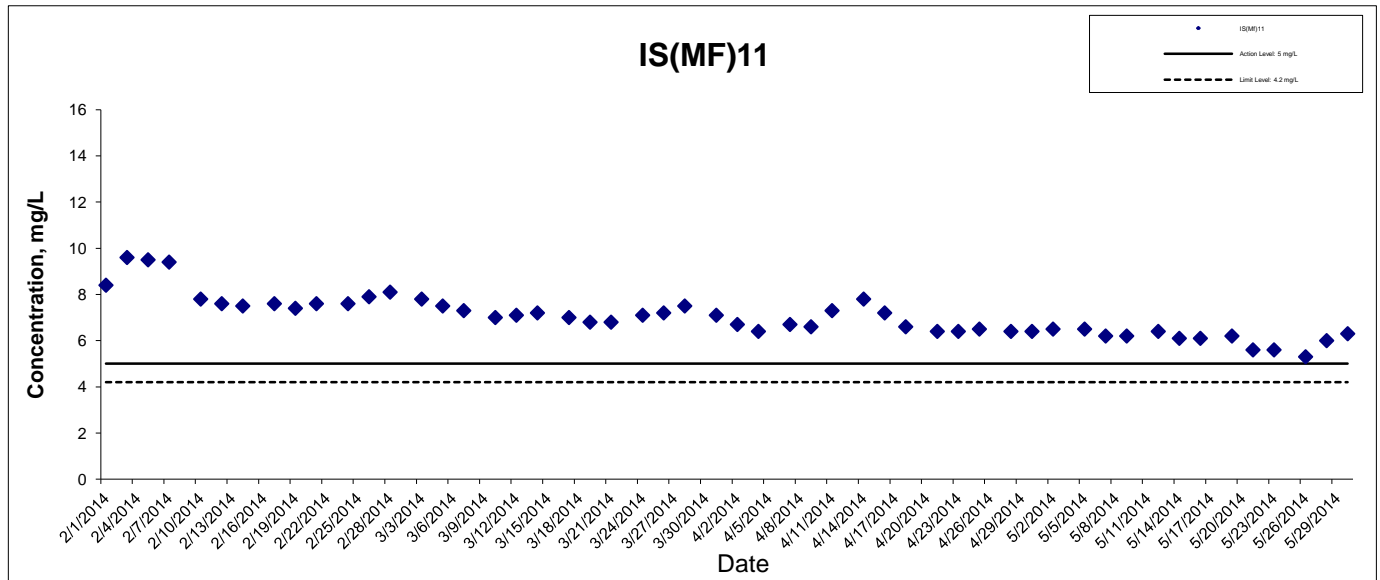




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

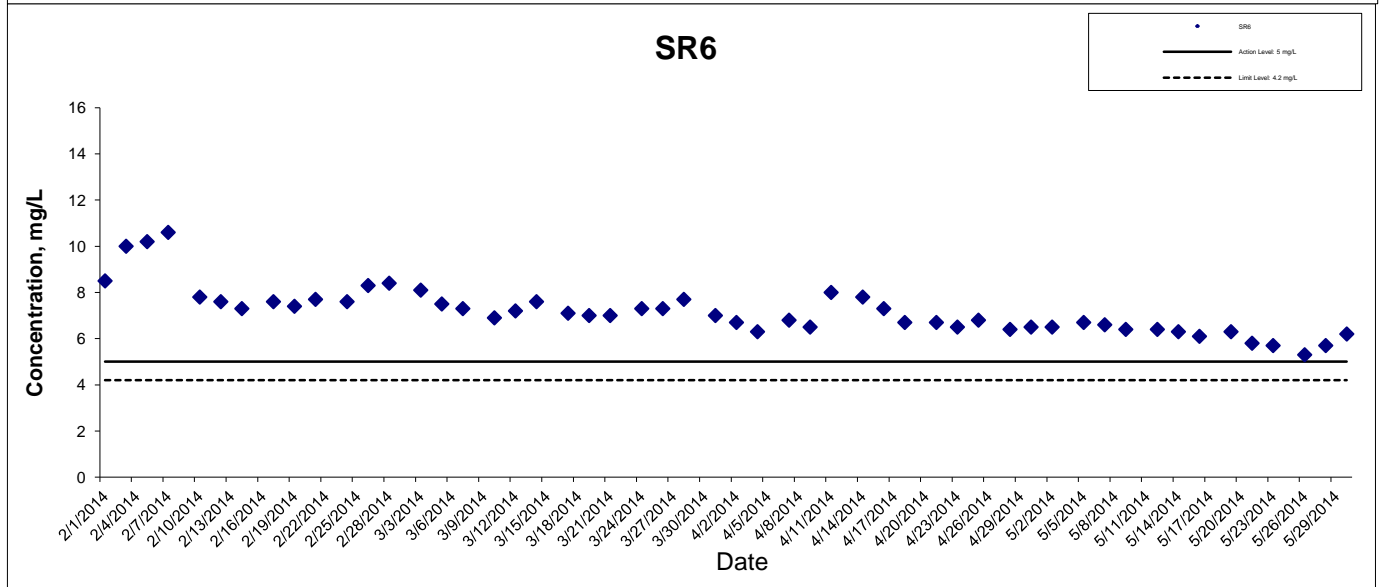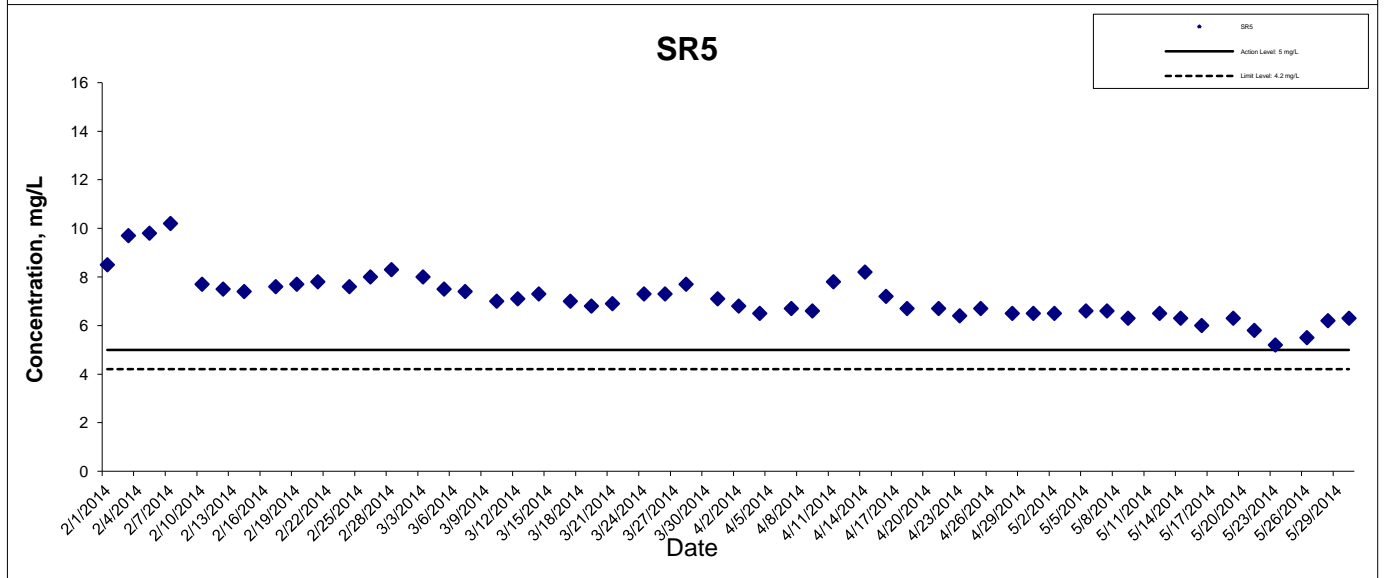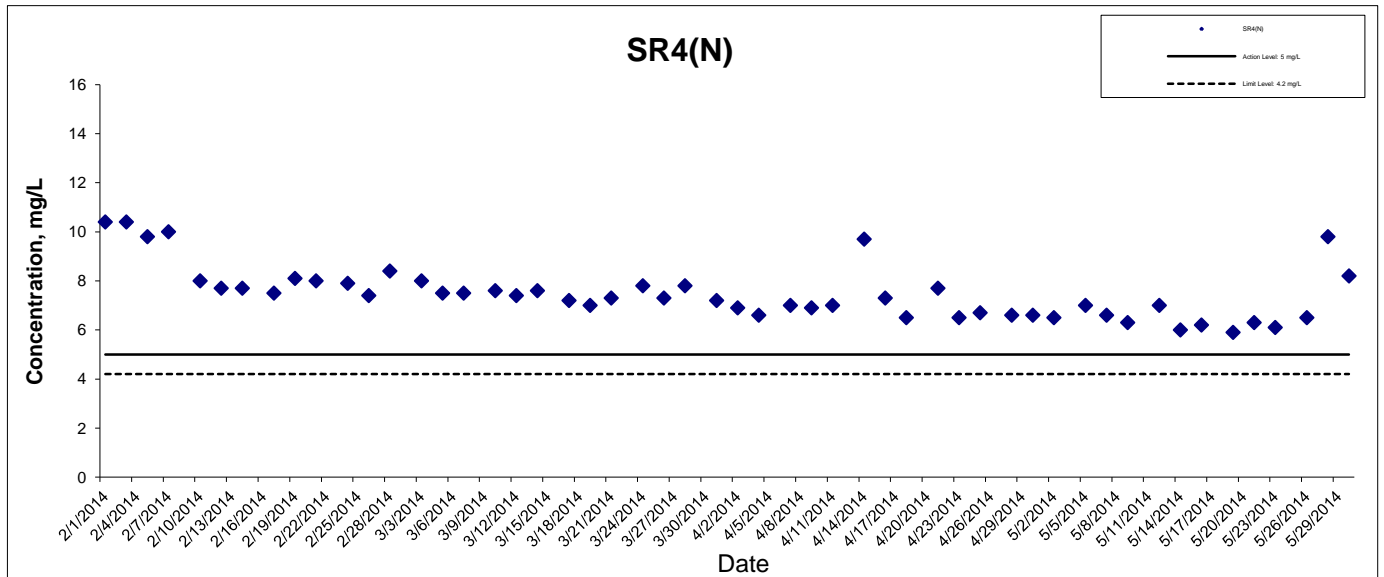


This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Ebb Tide

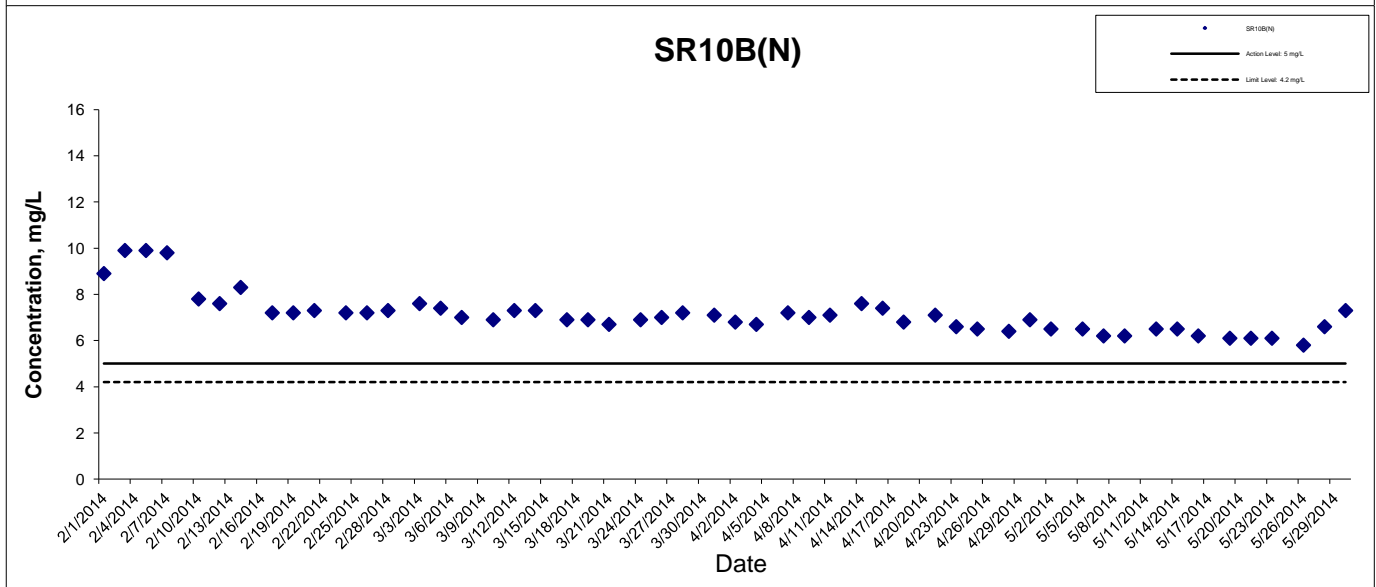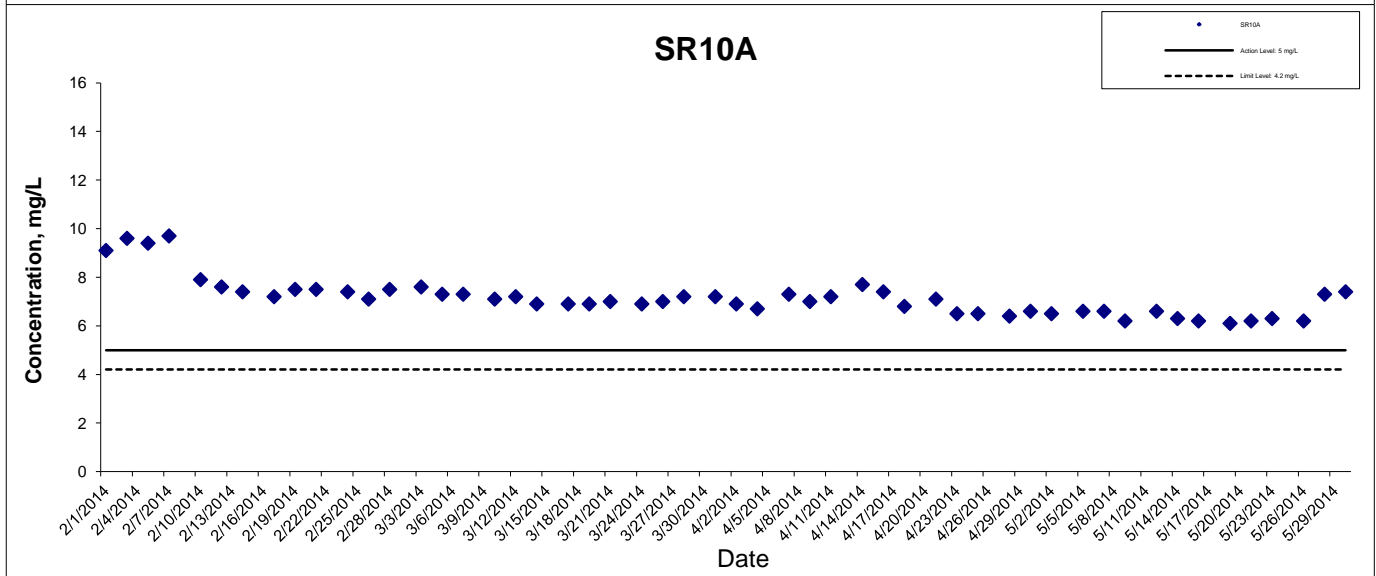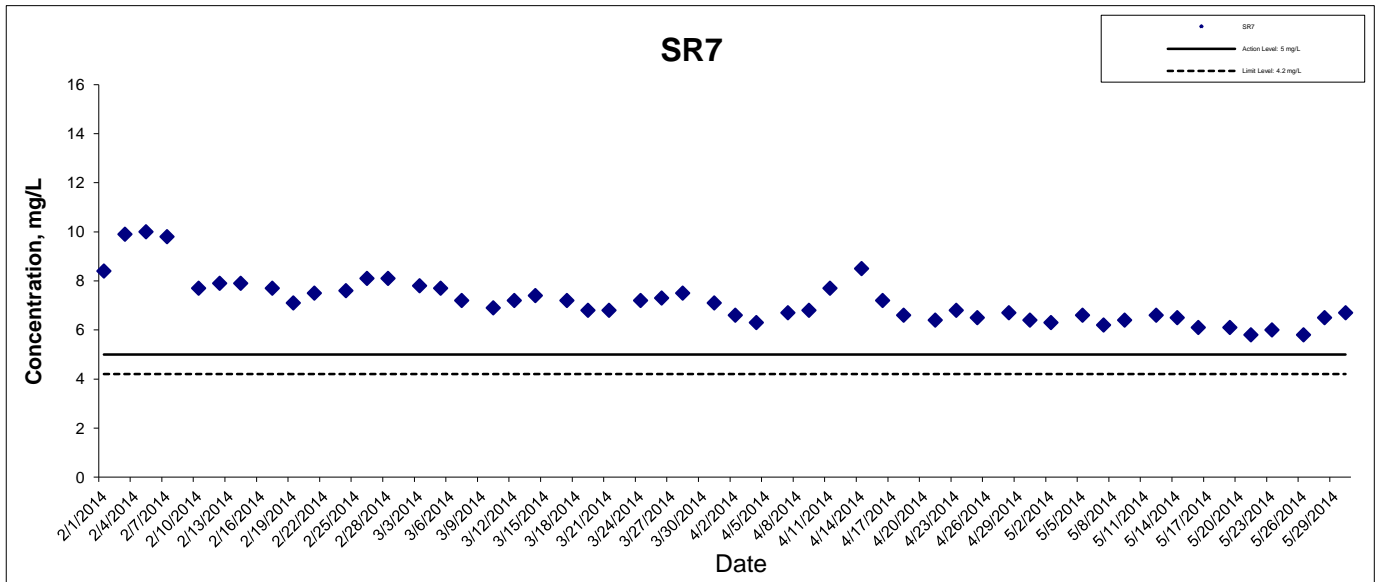




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

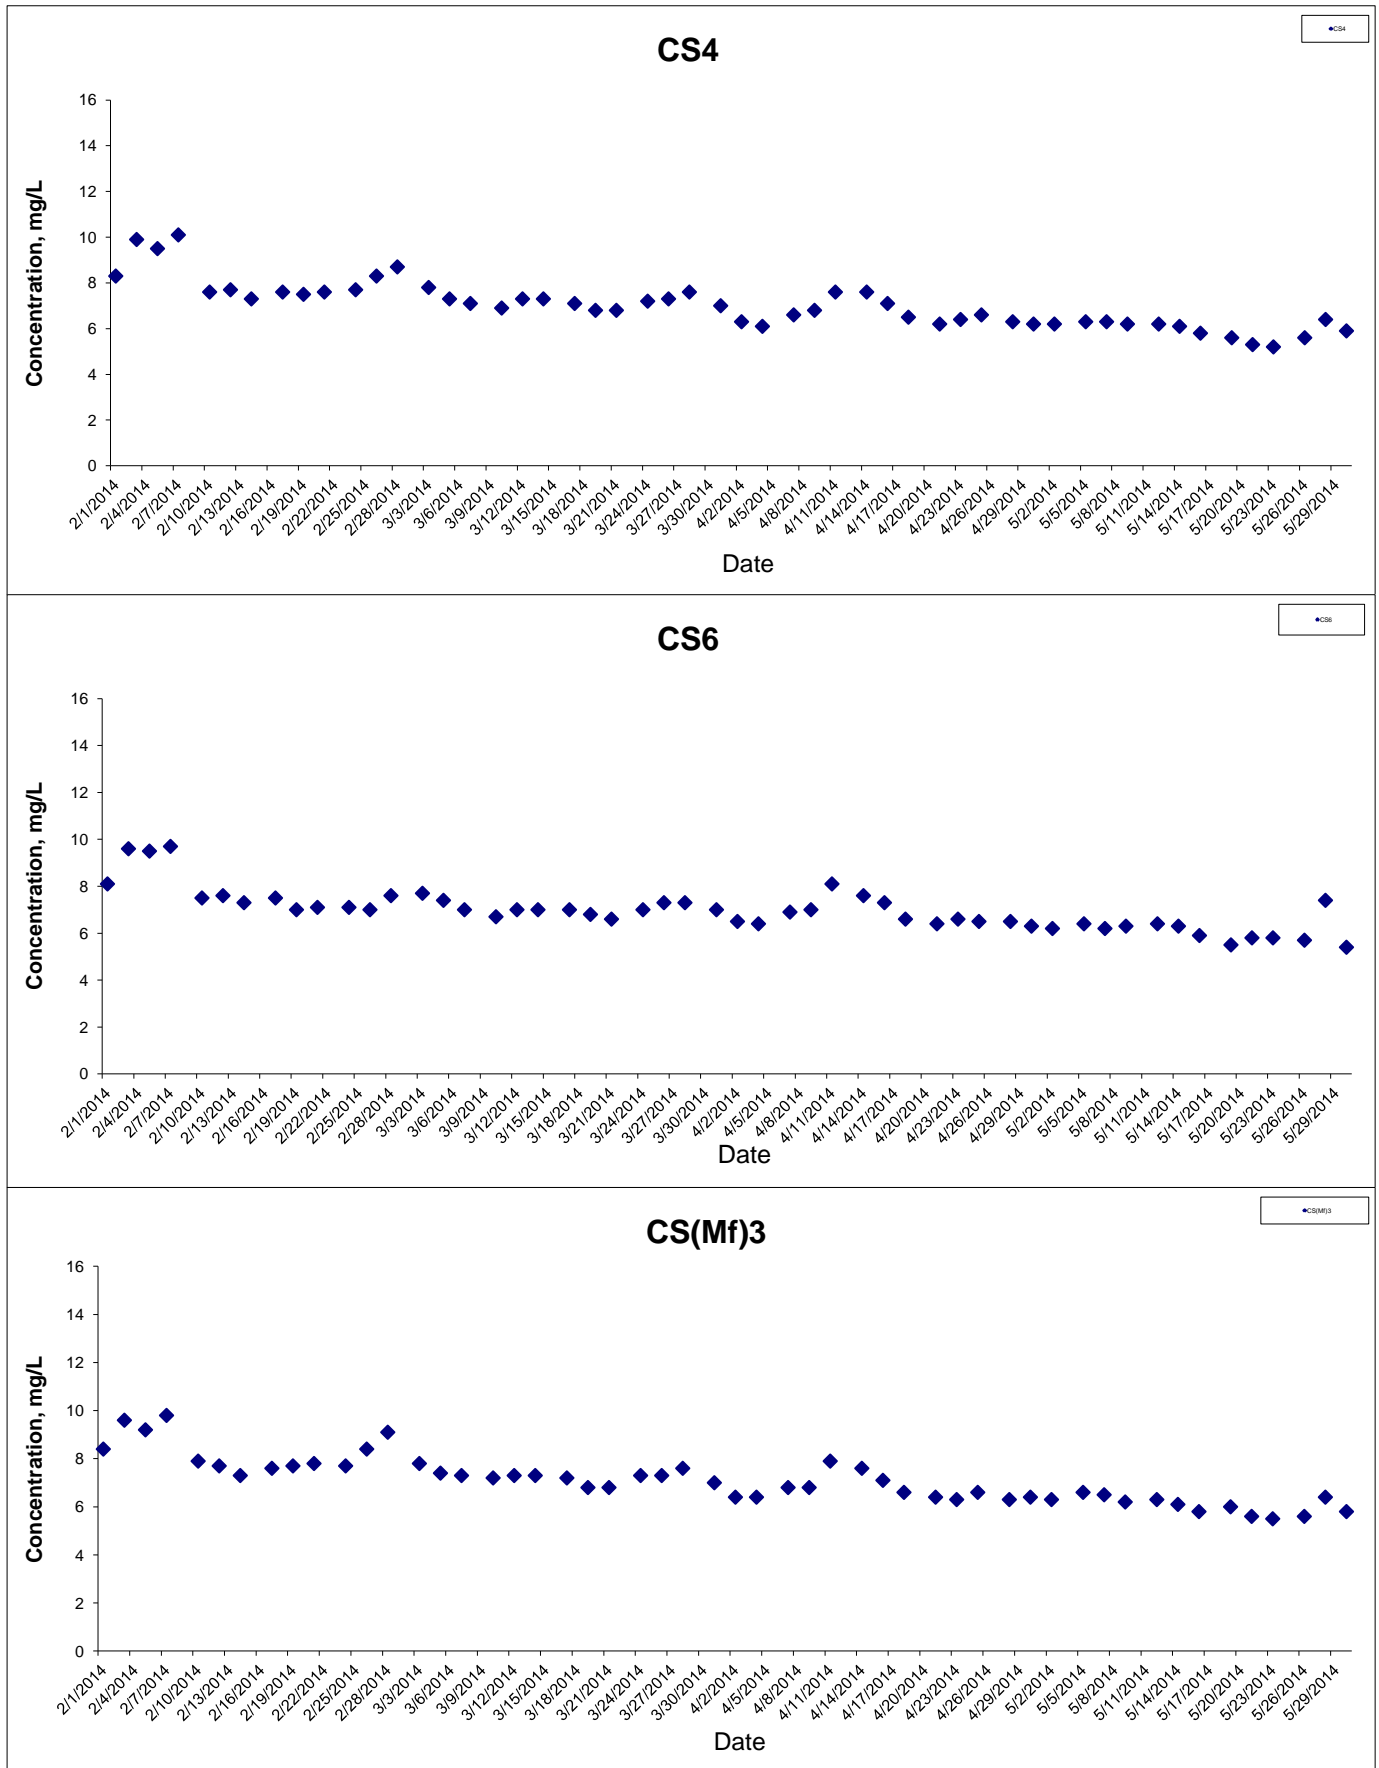




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

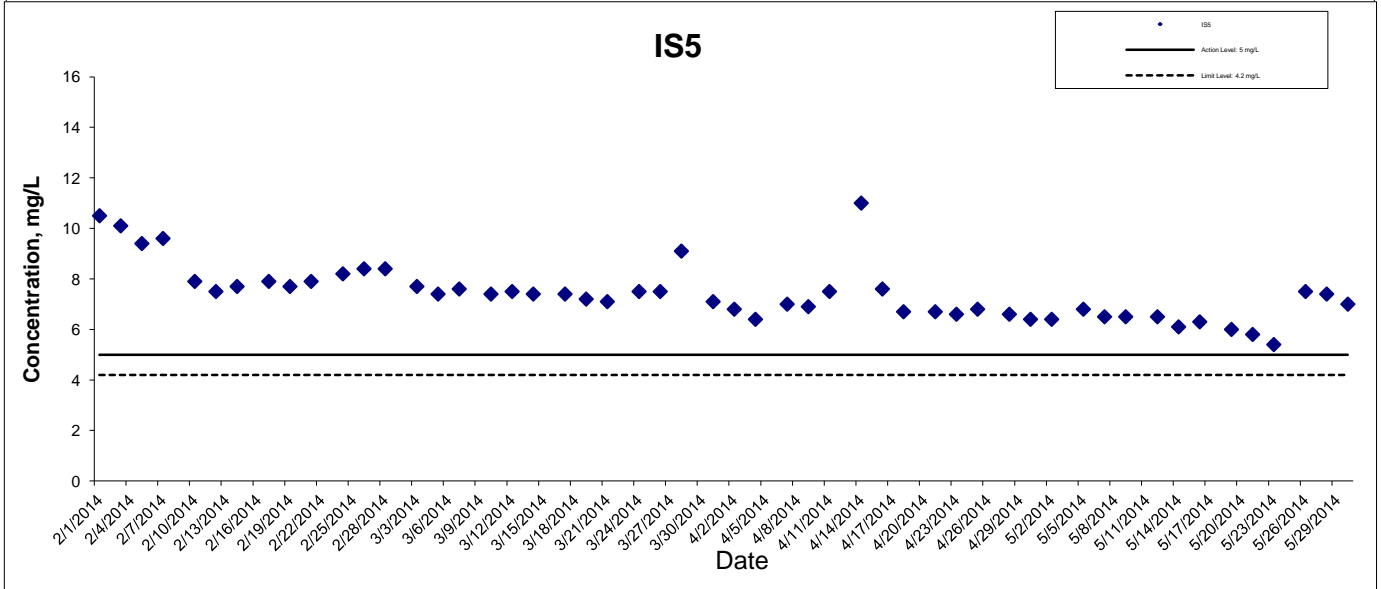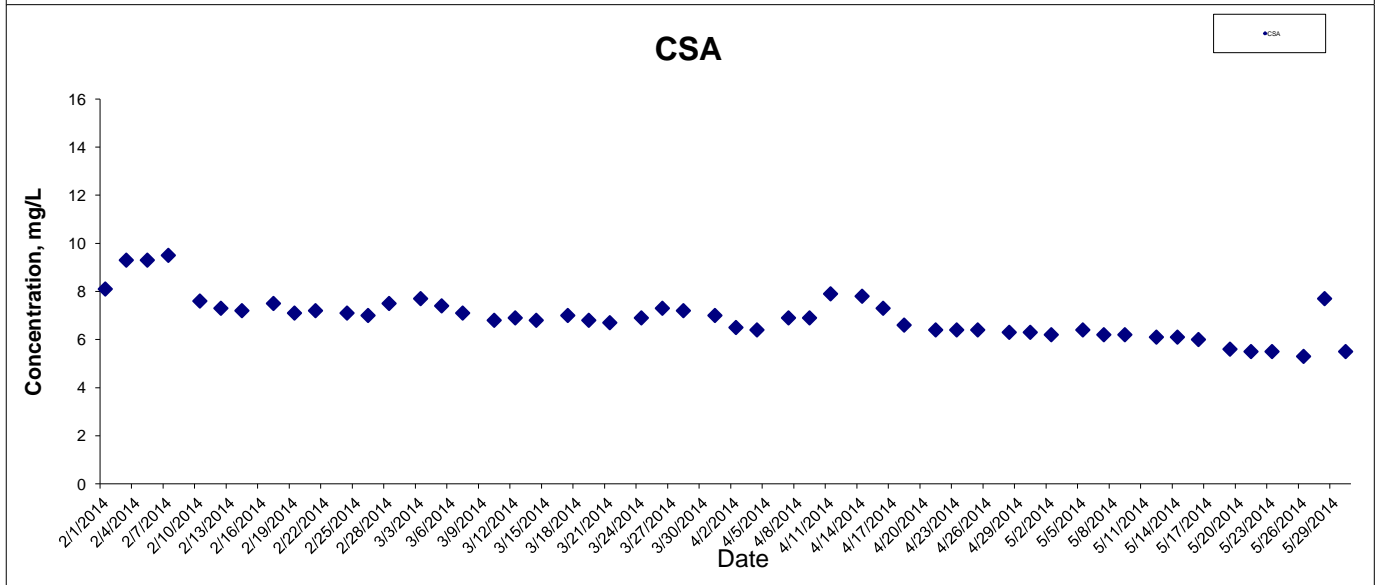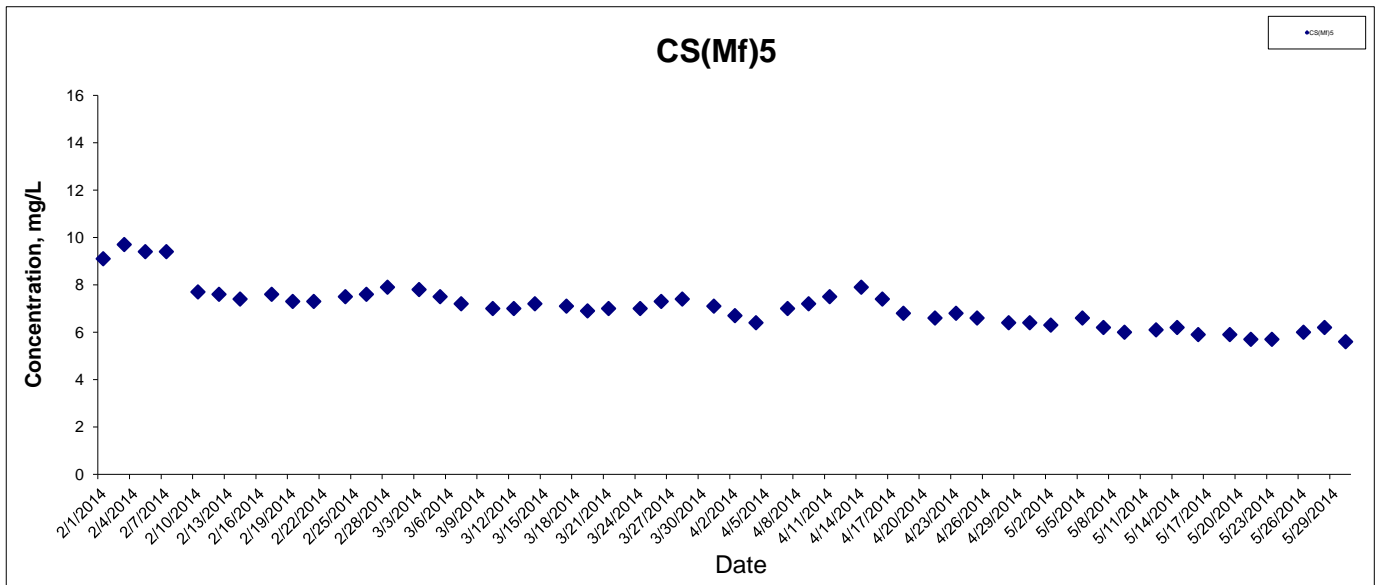


This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

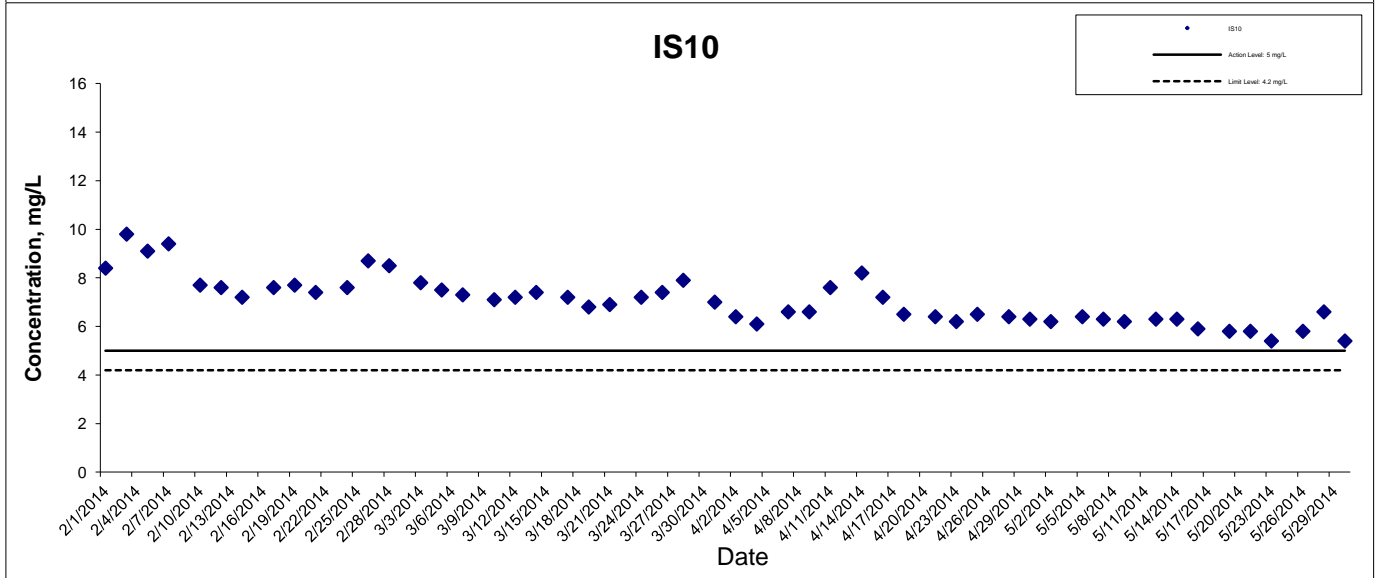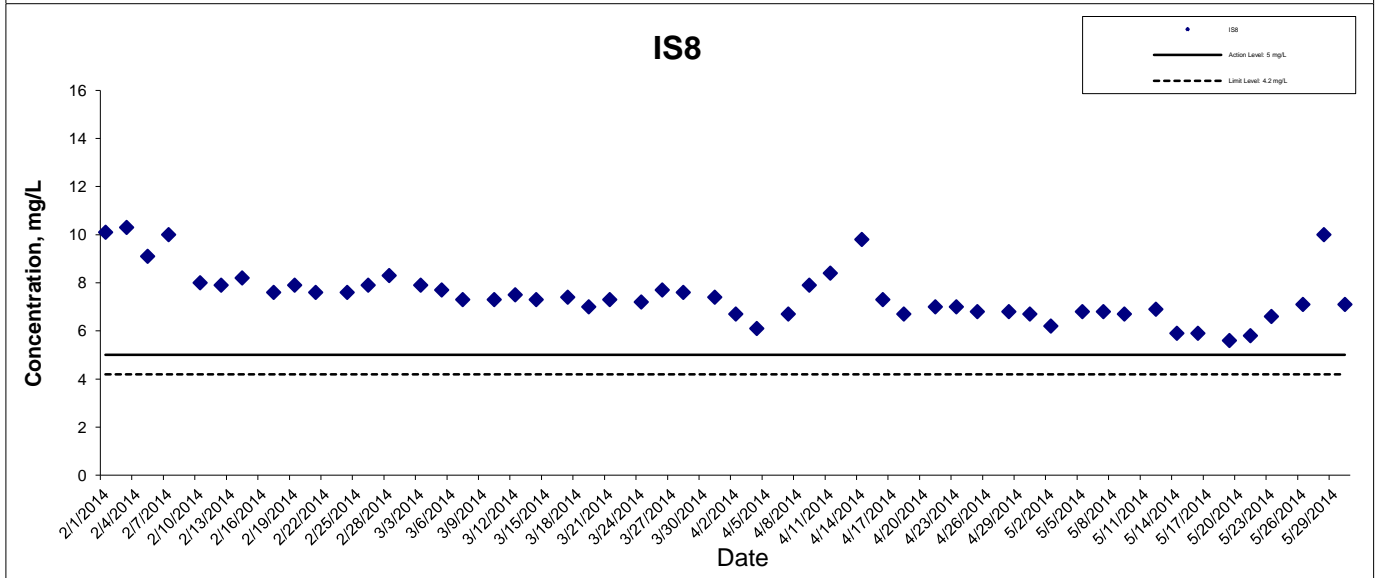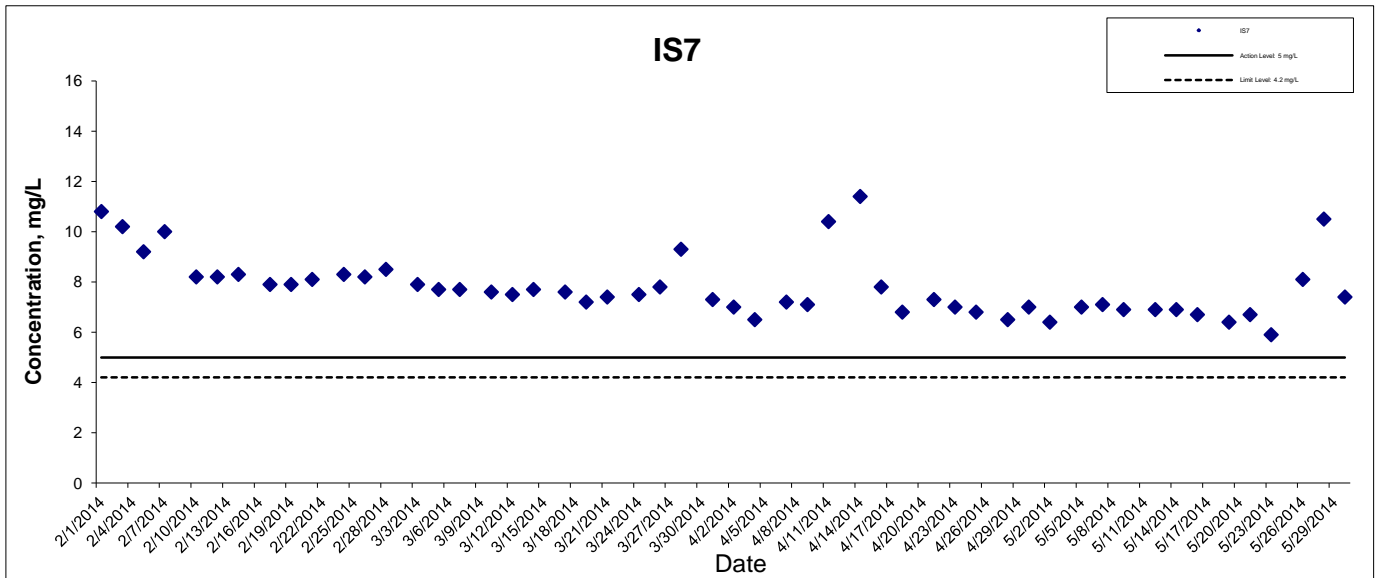

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.




Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

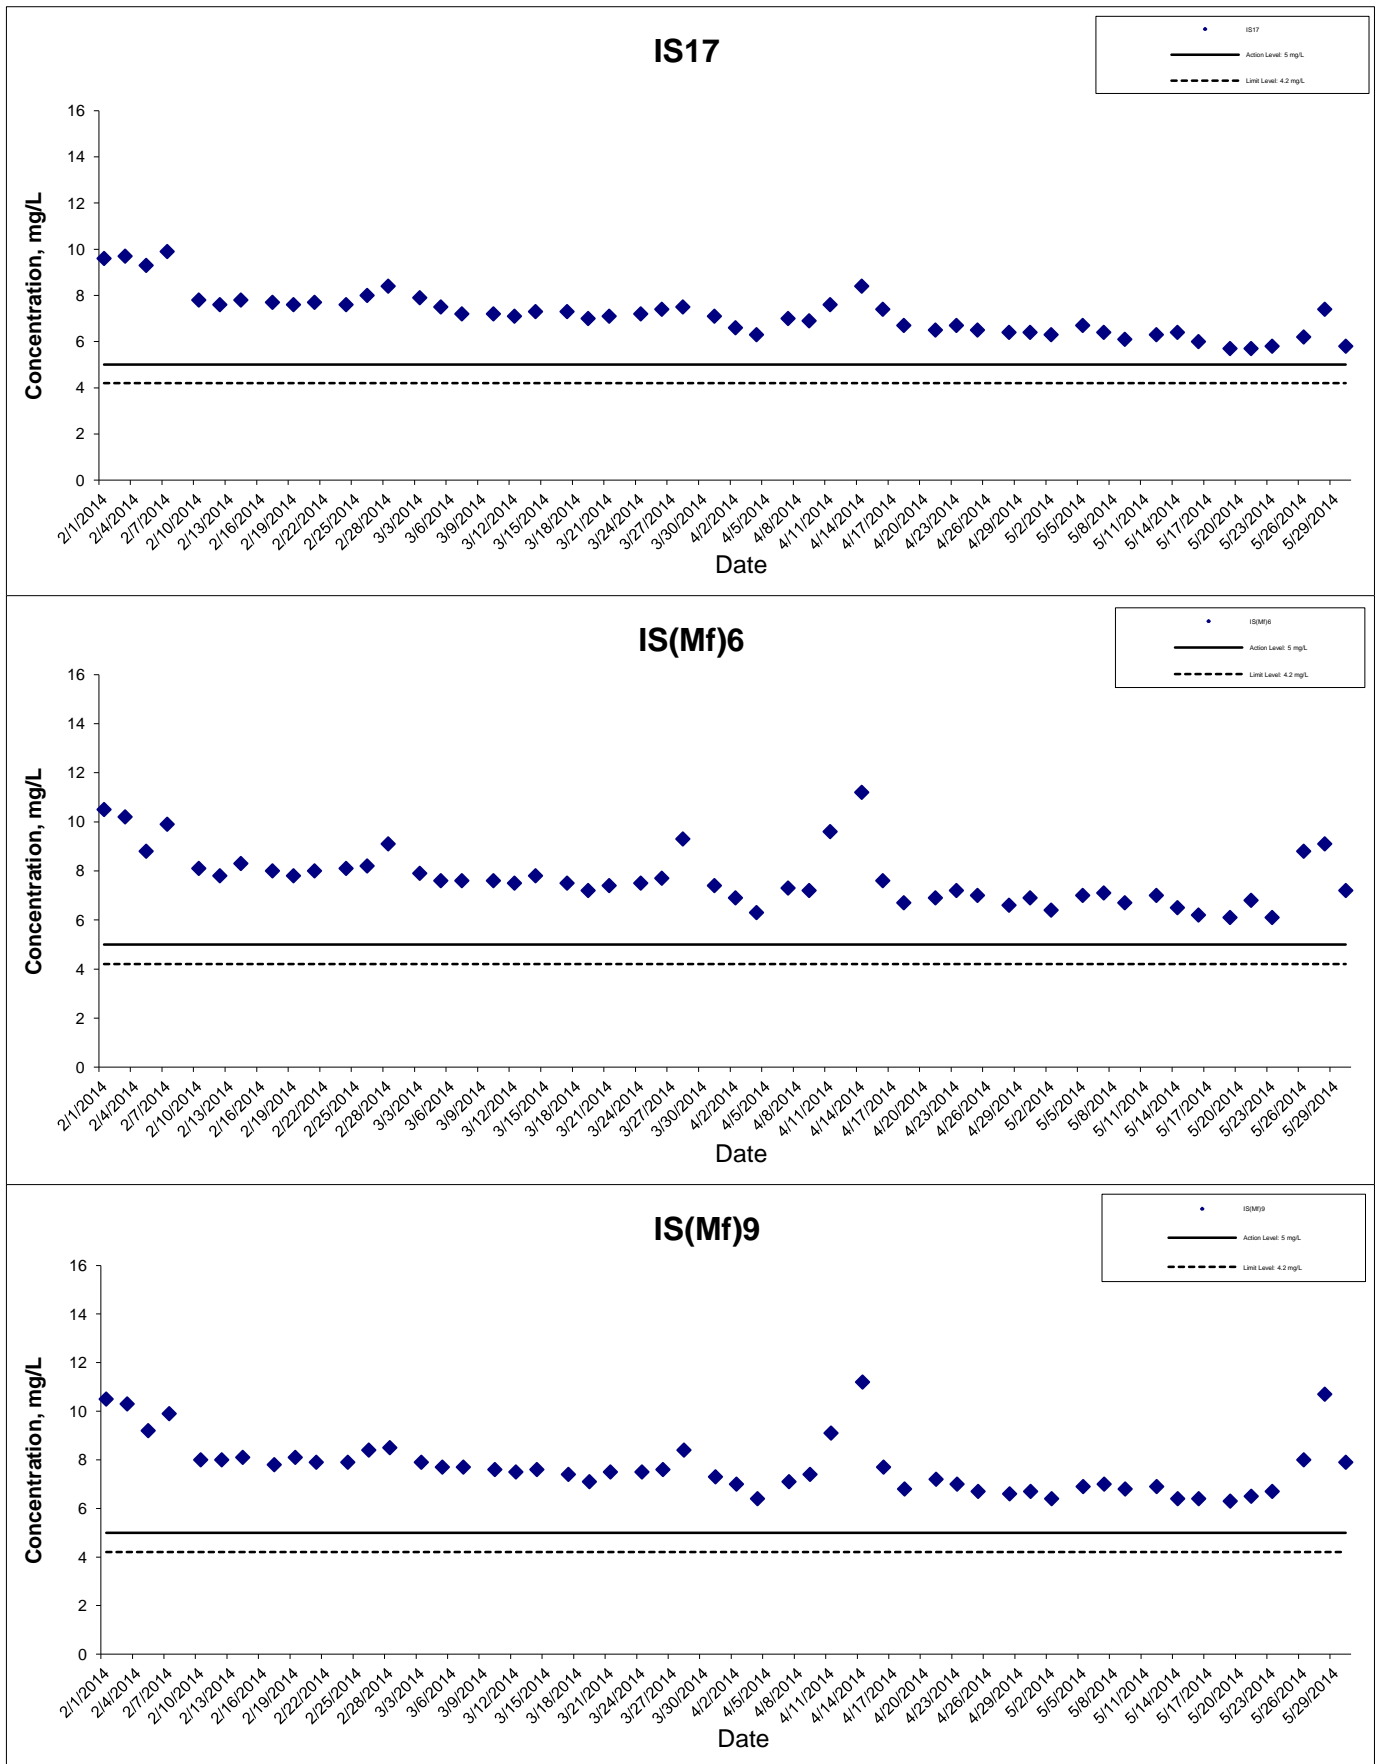

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.






Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

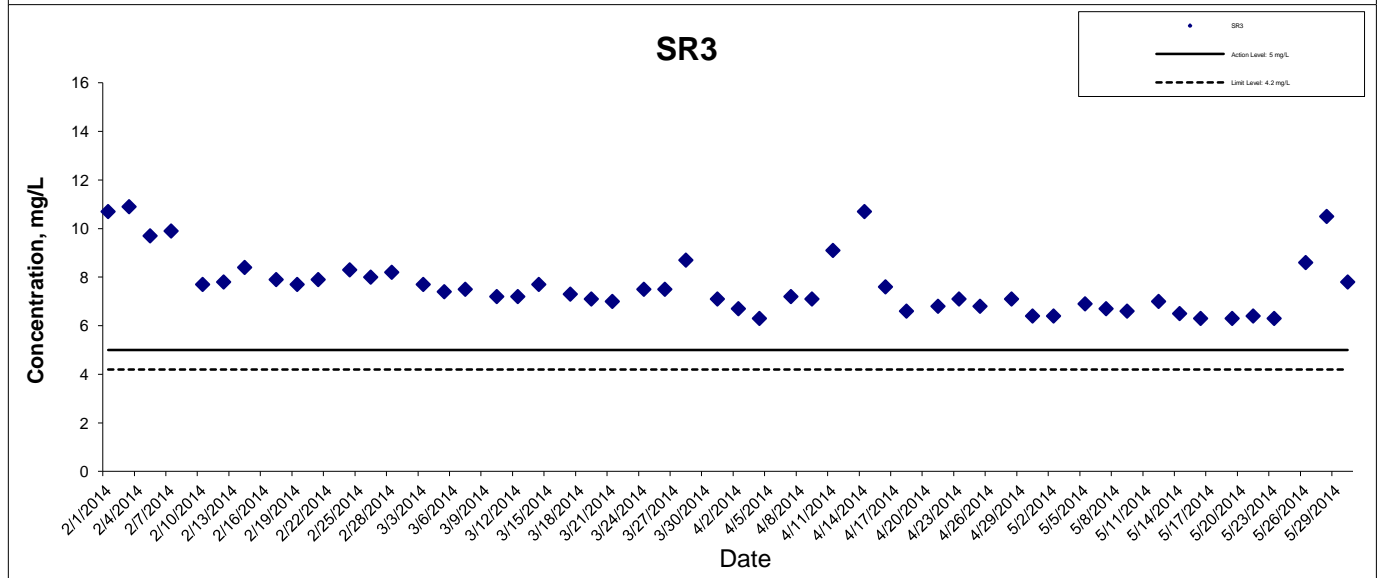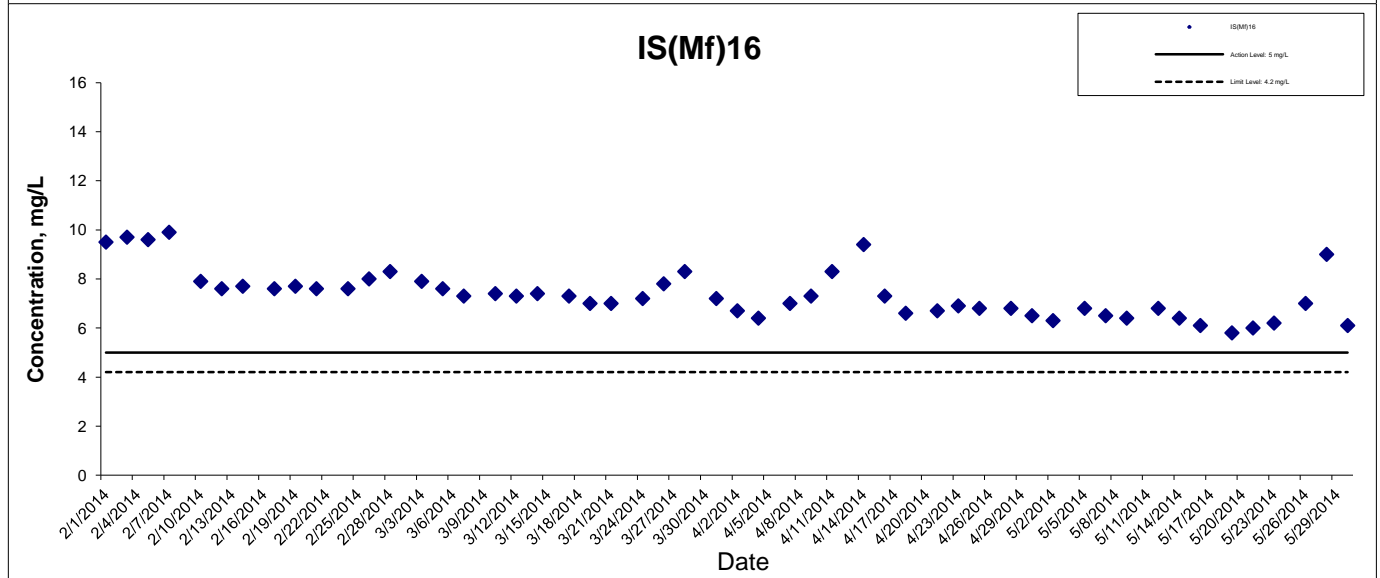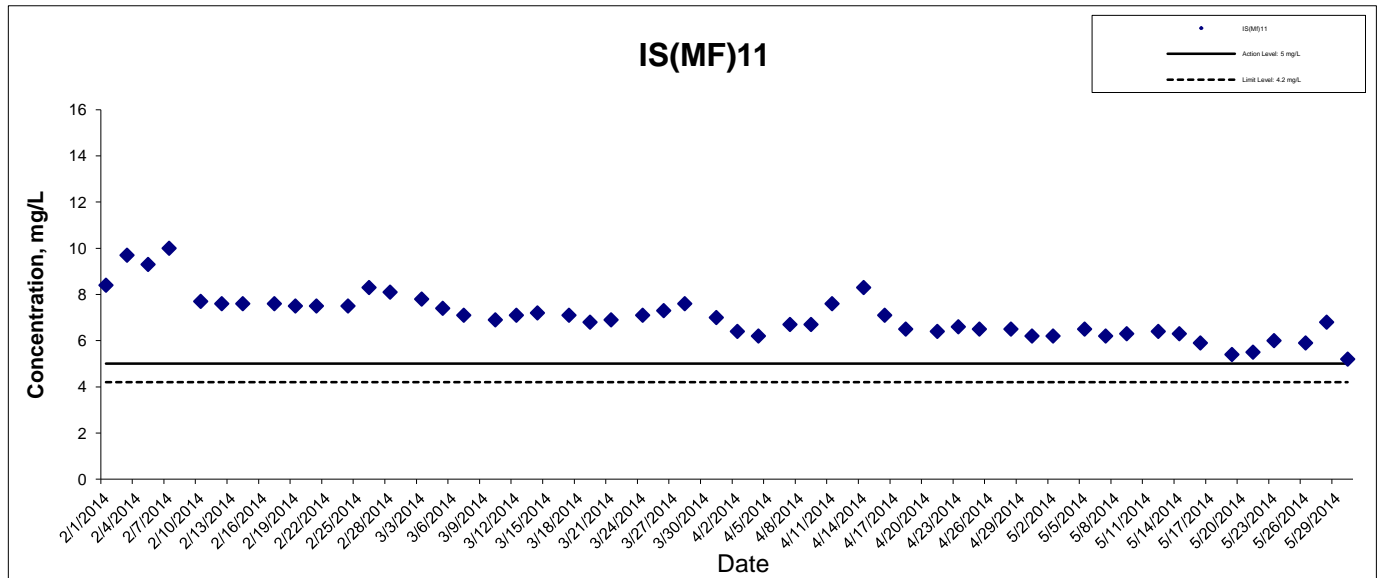




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

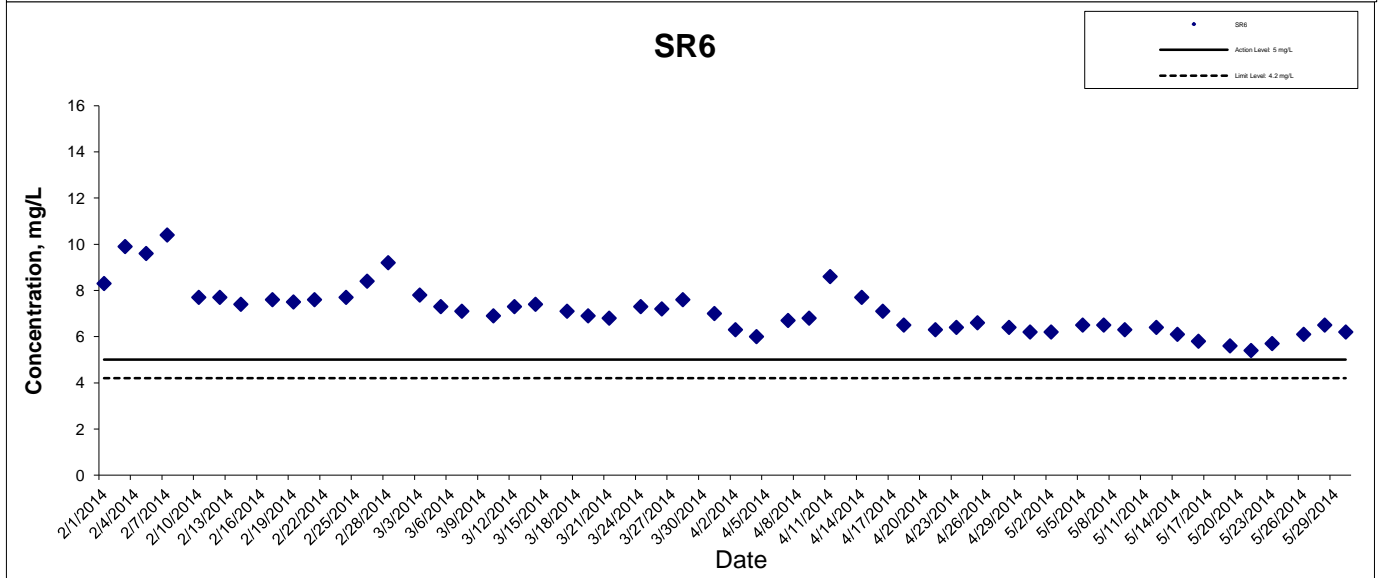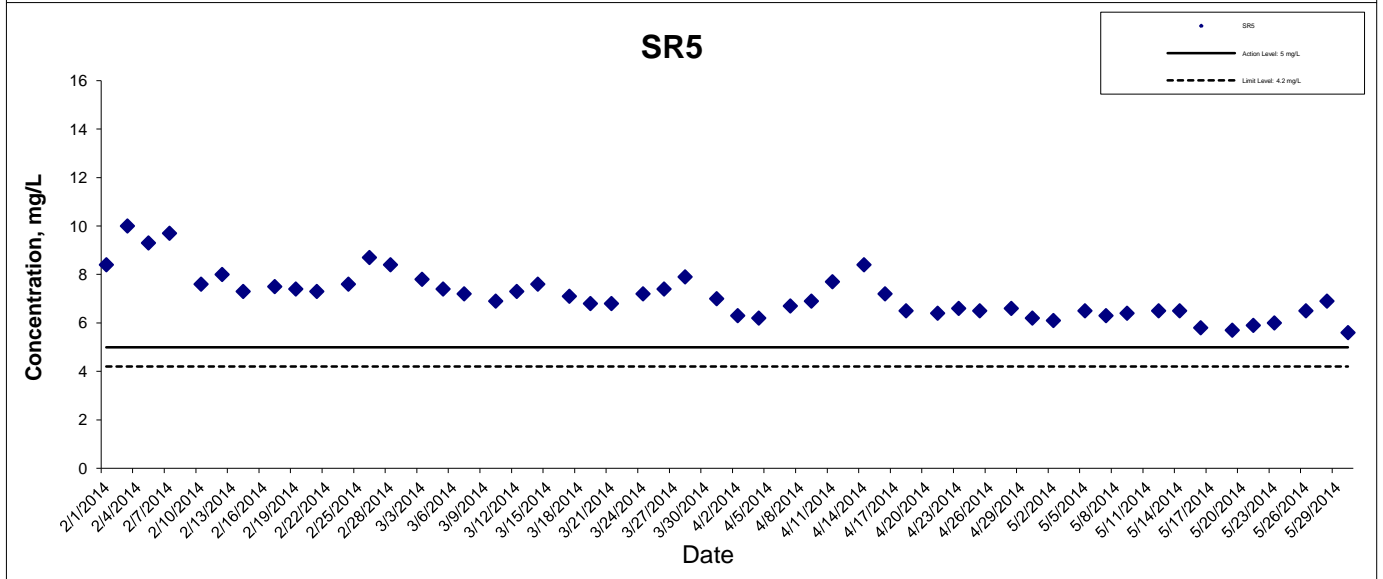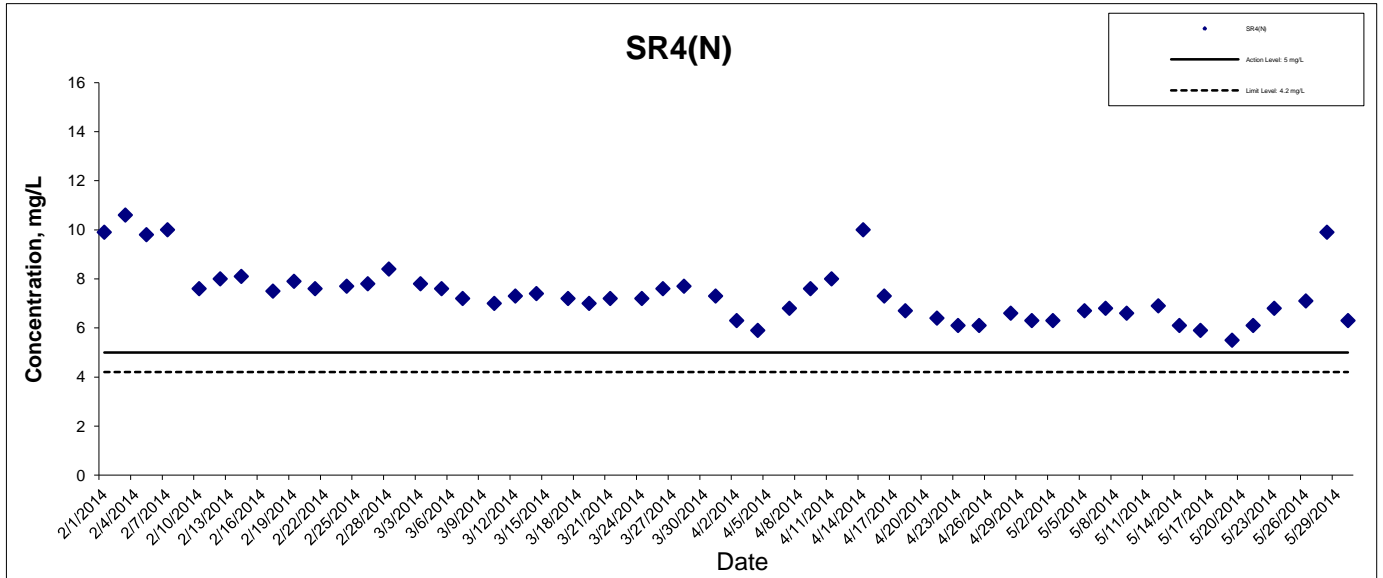




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Dissolved Oxygen (Surface & Middle) at Mid-Flood Tide

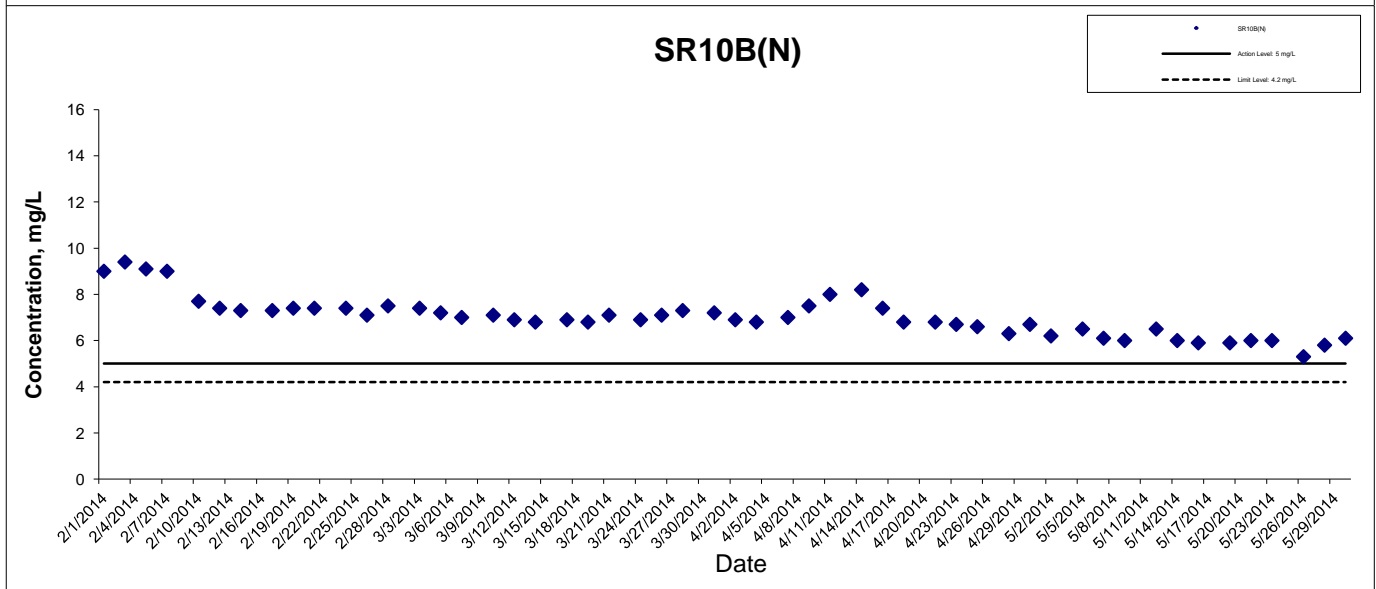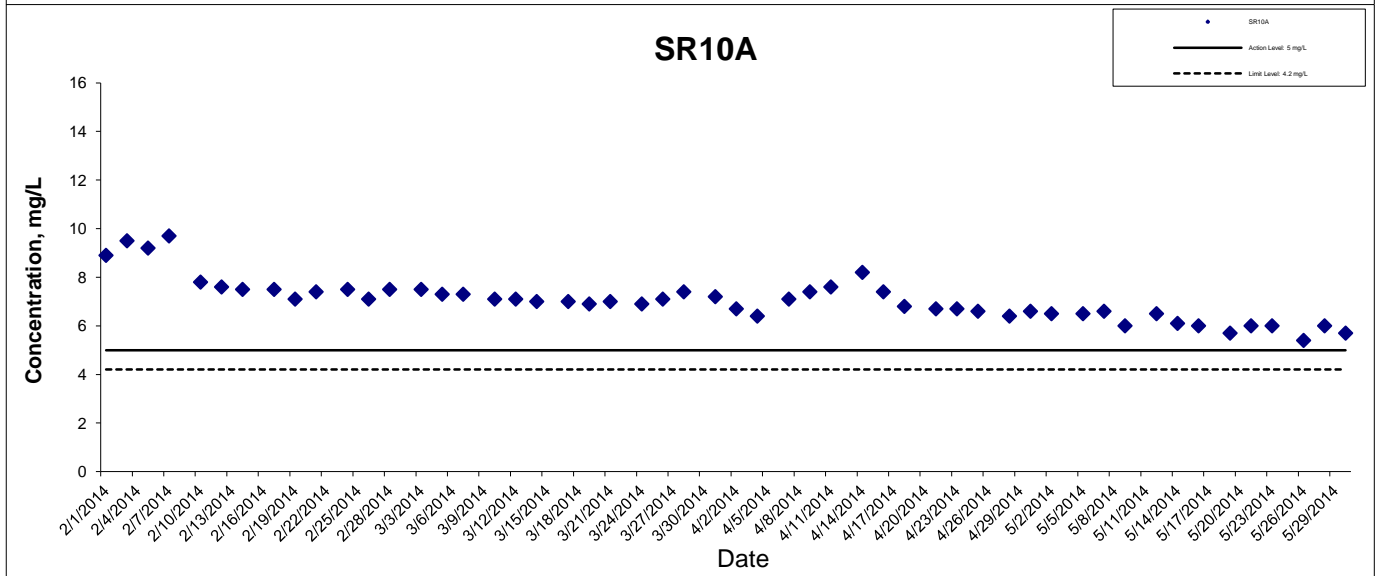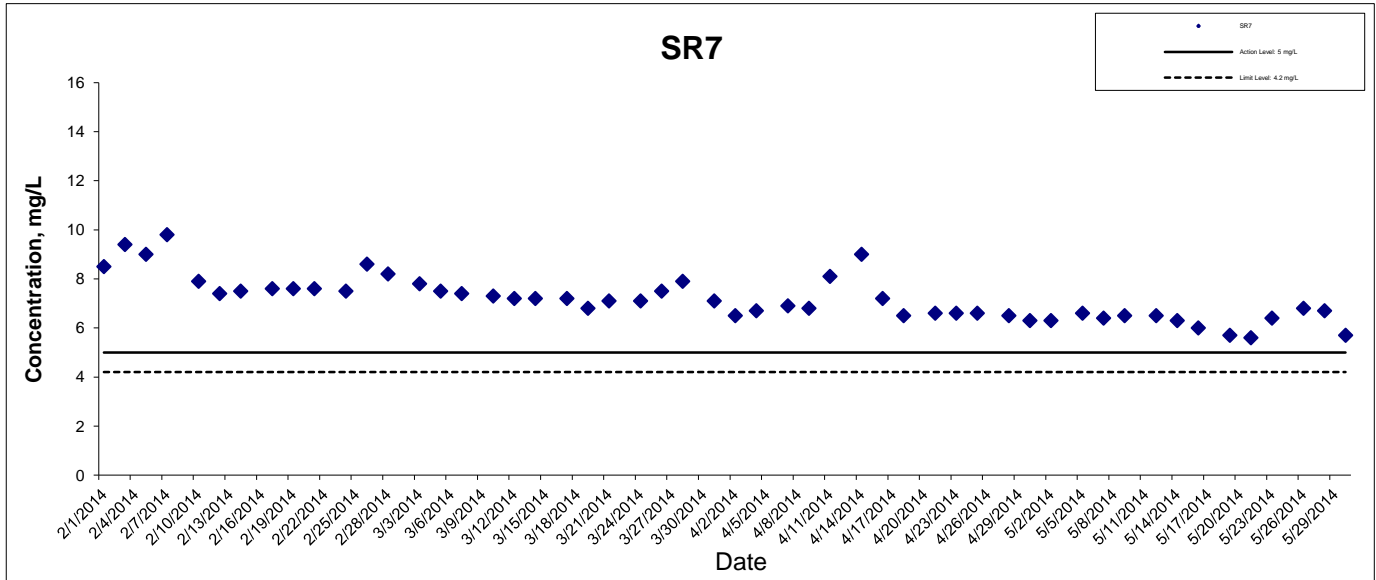




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

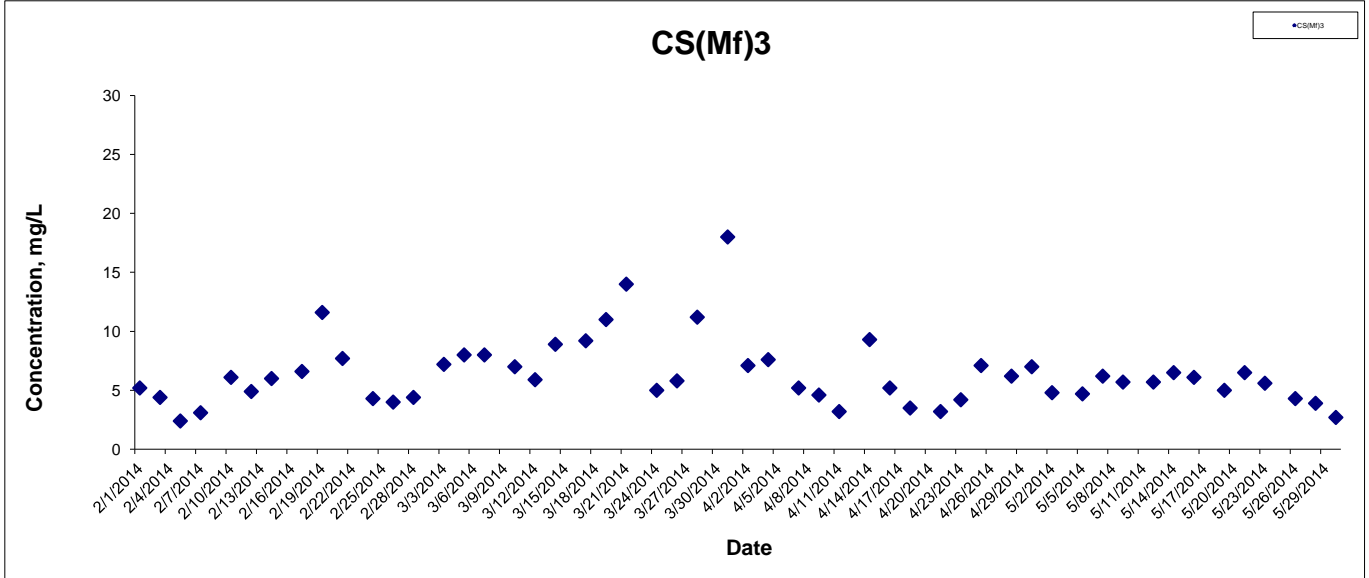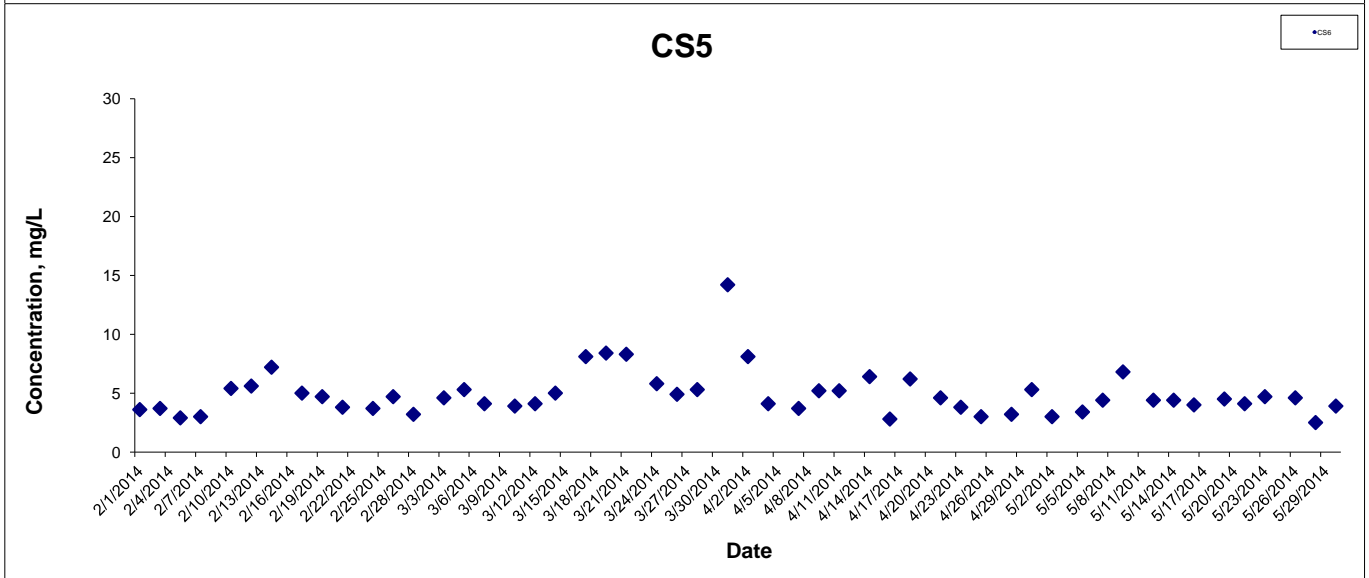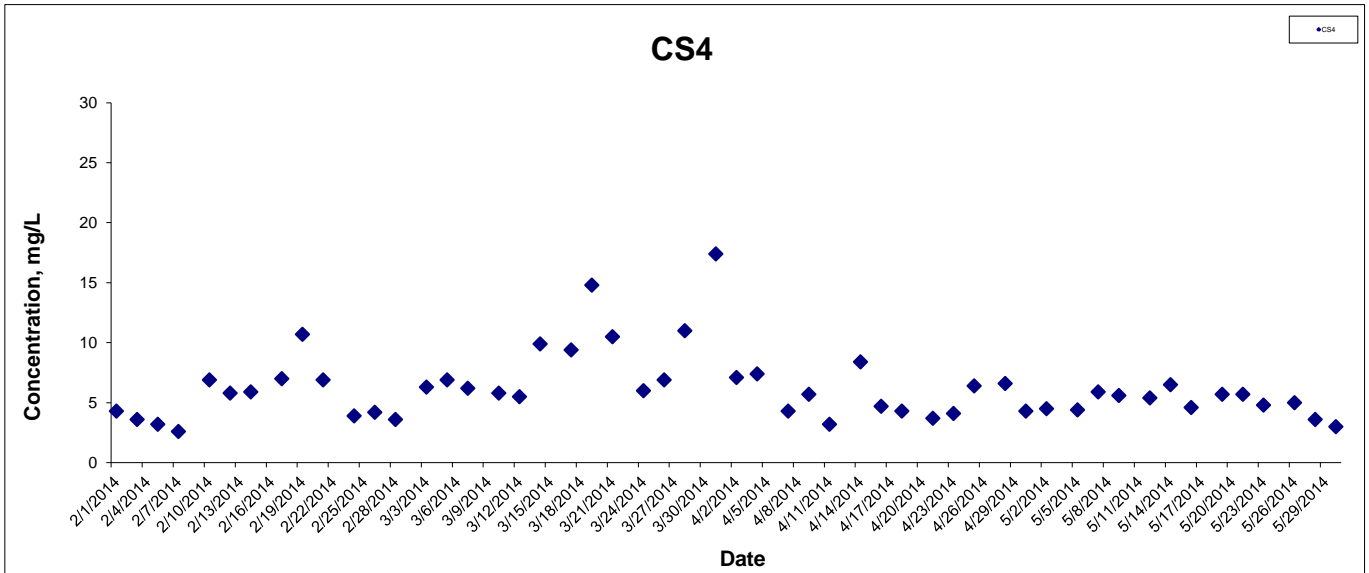




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

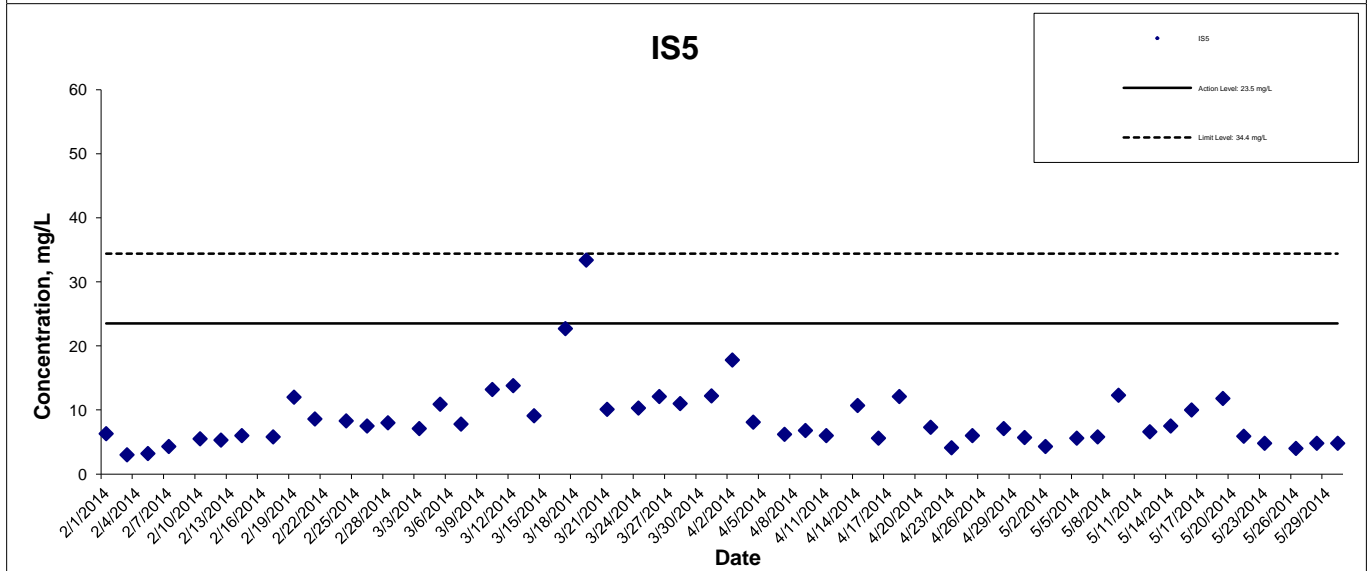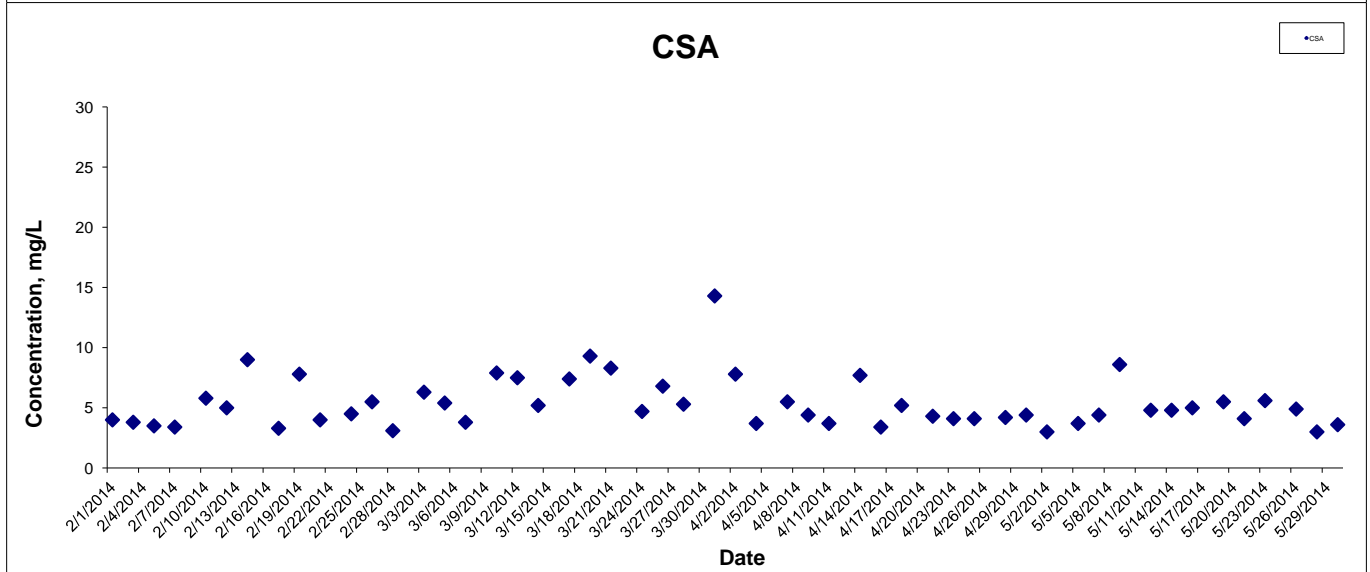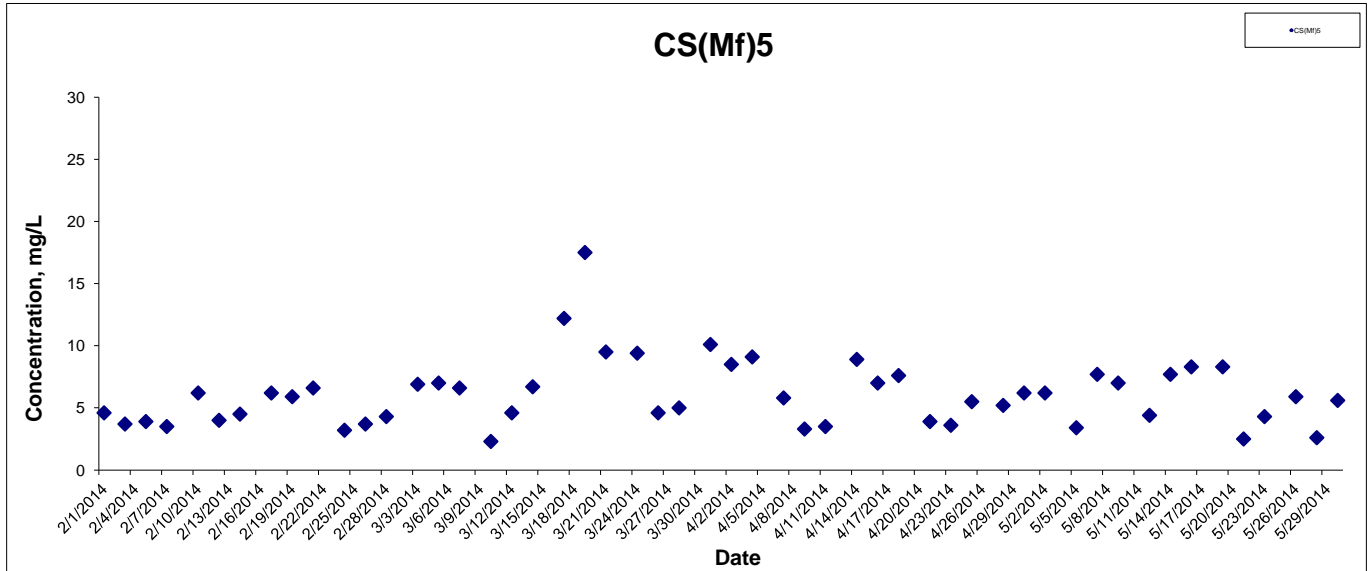




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

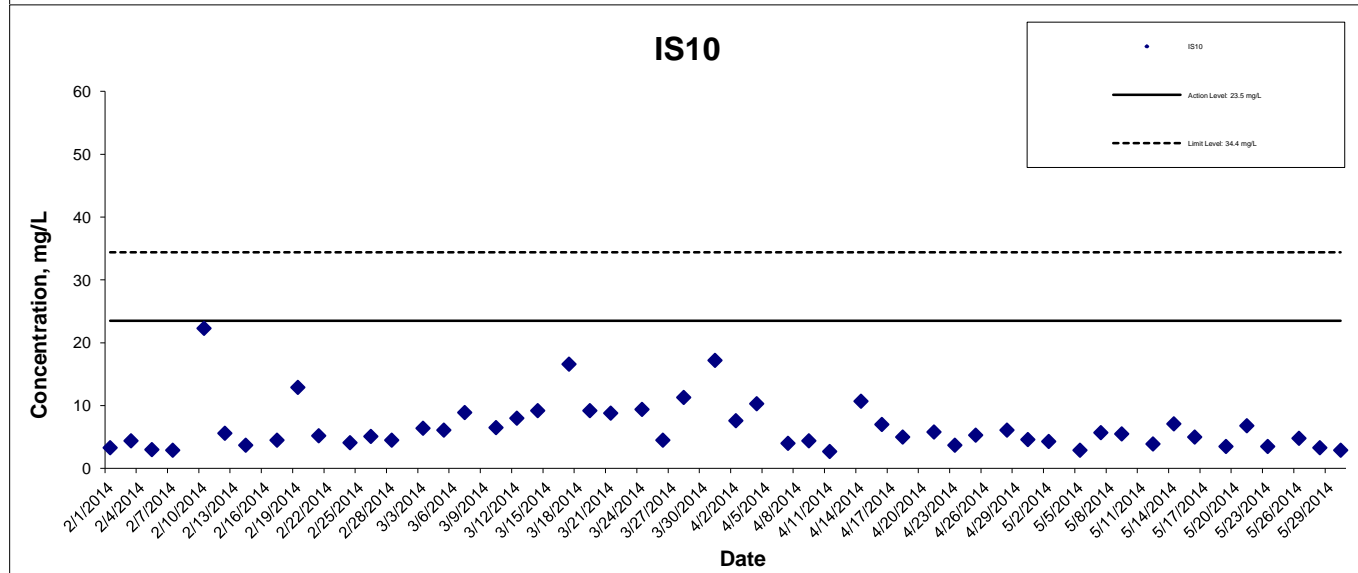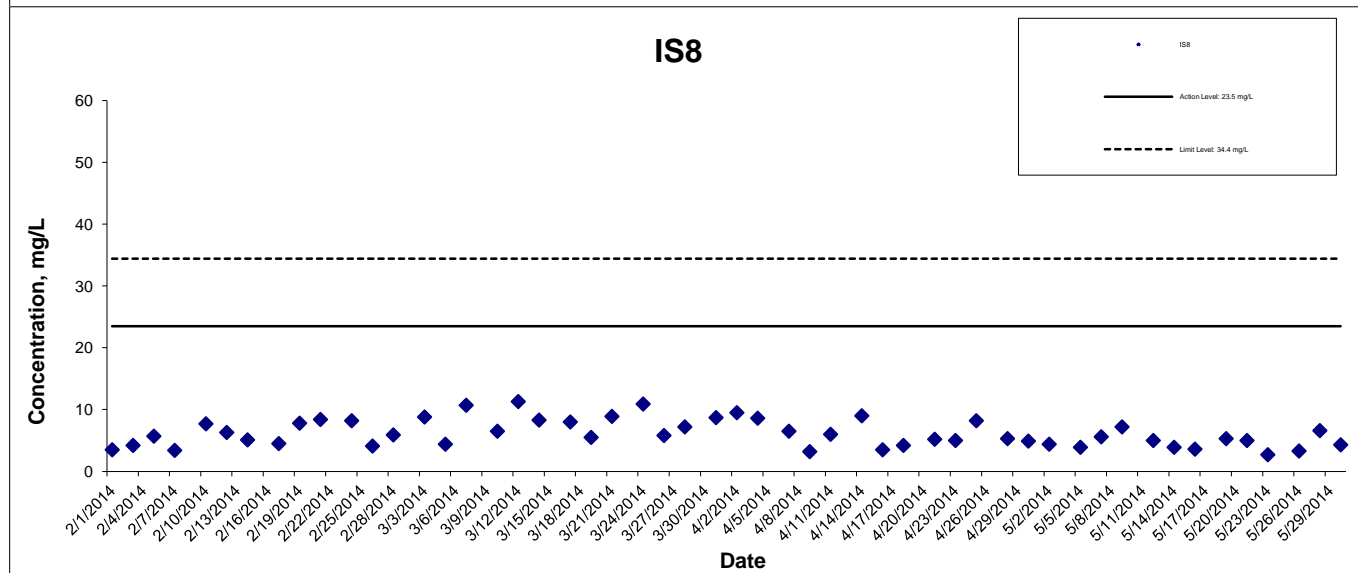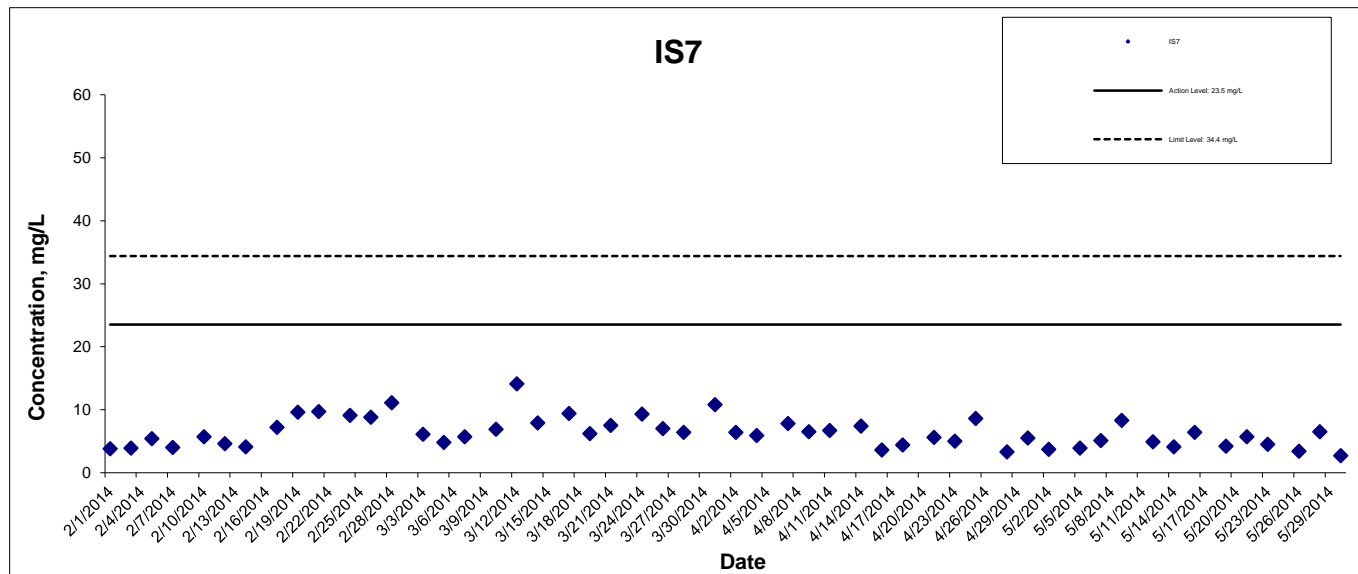




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

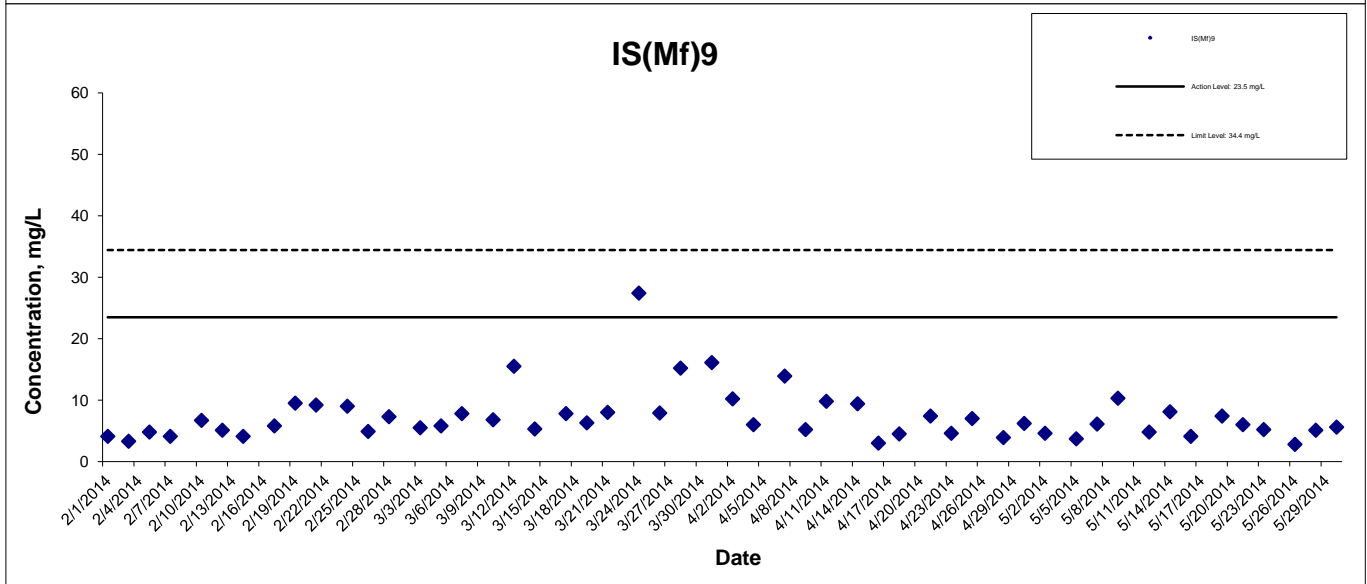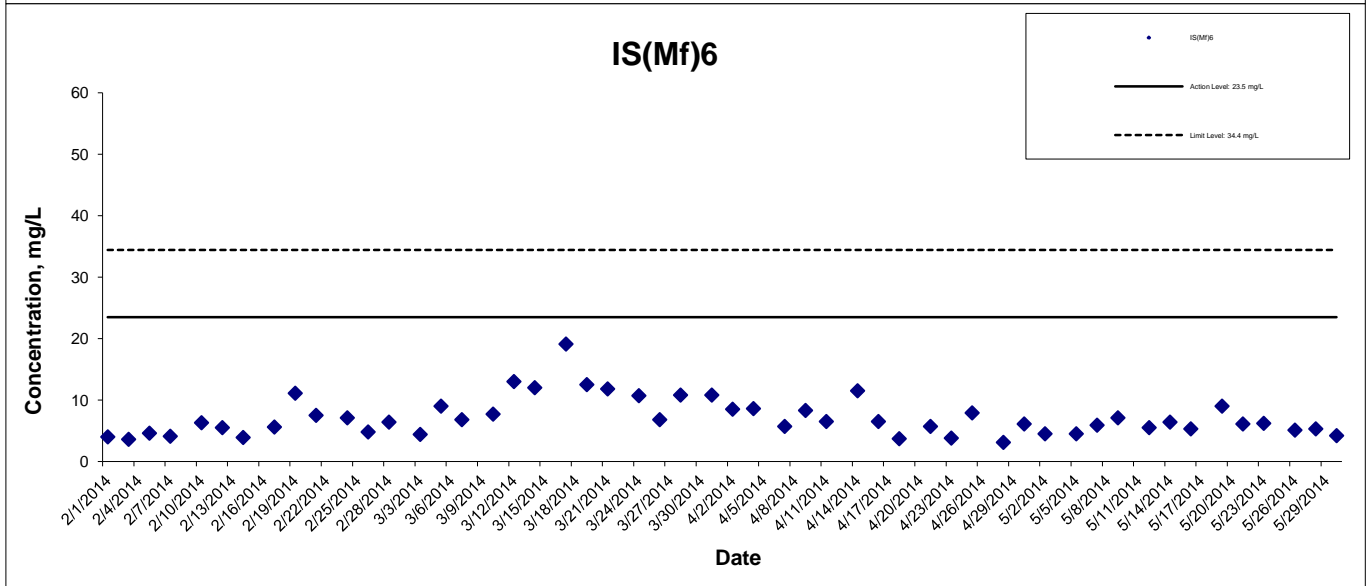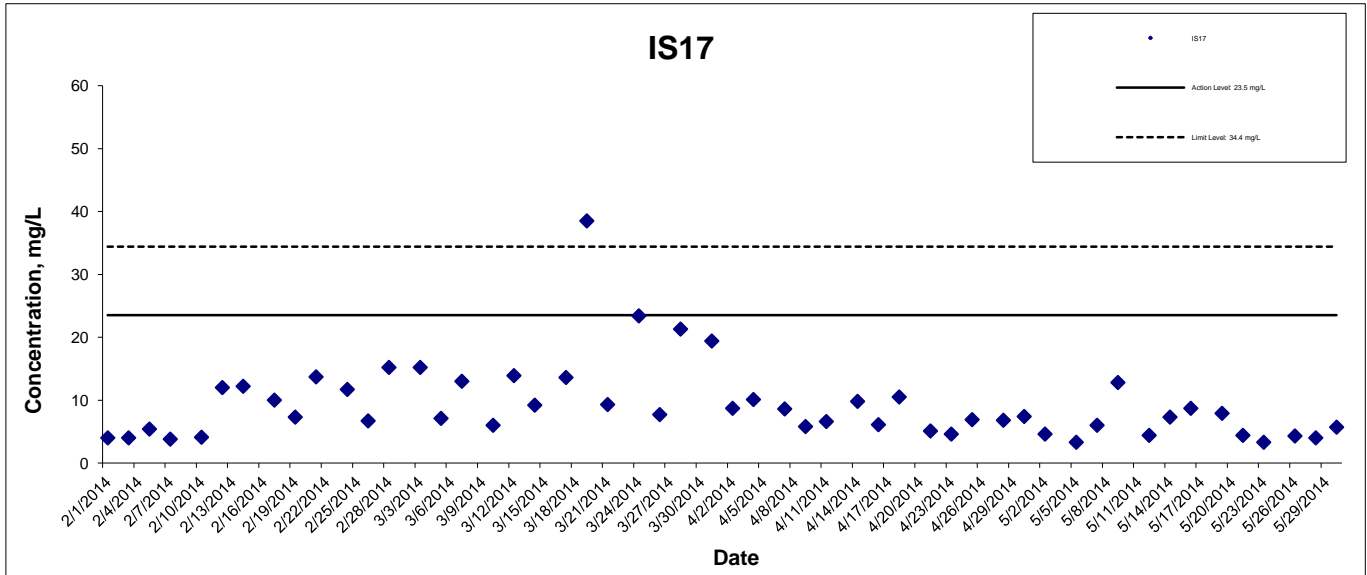




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

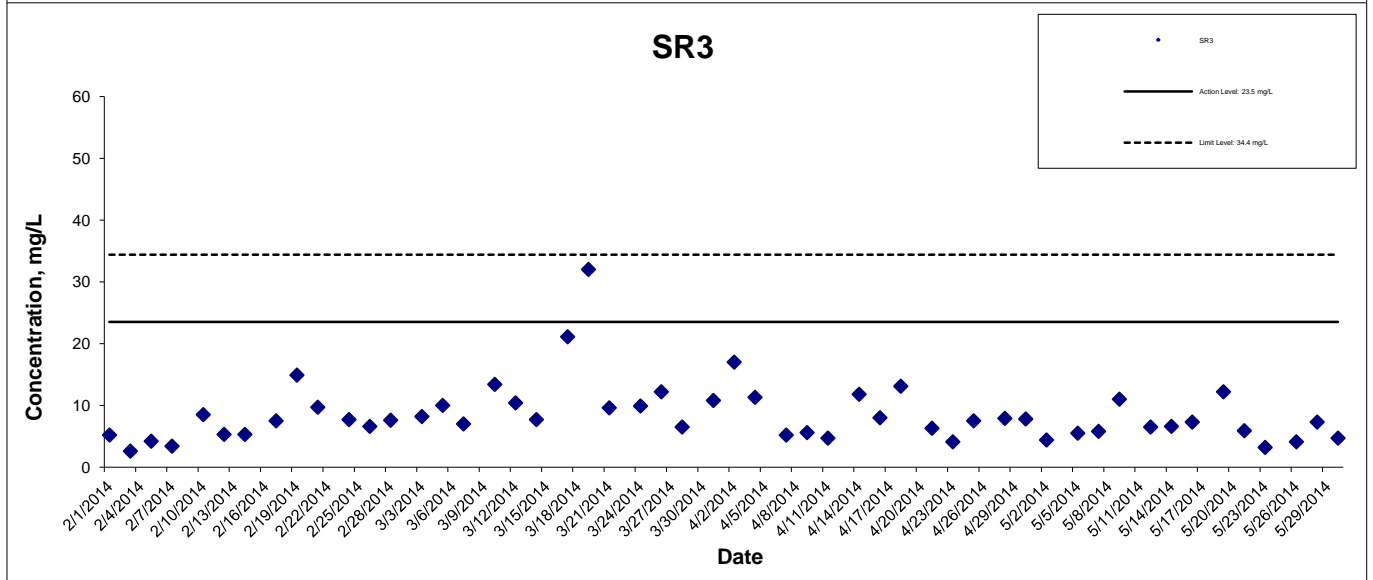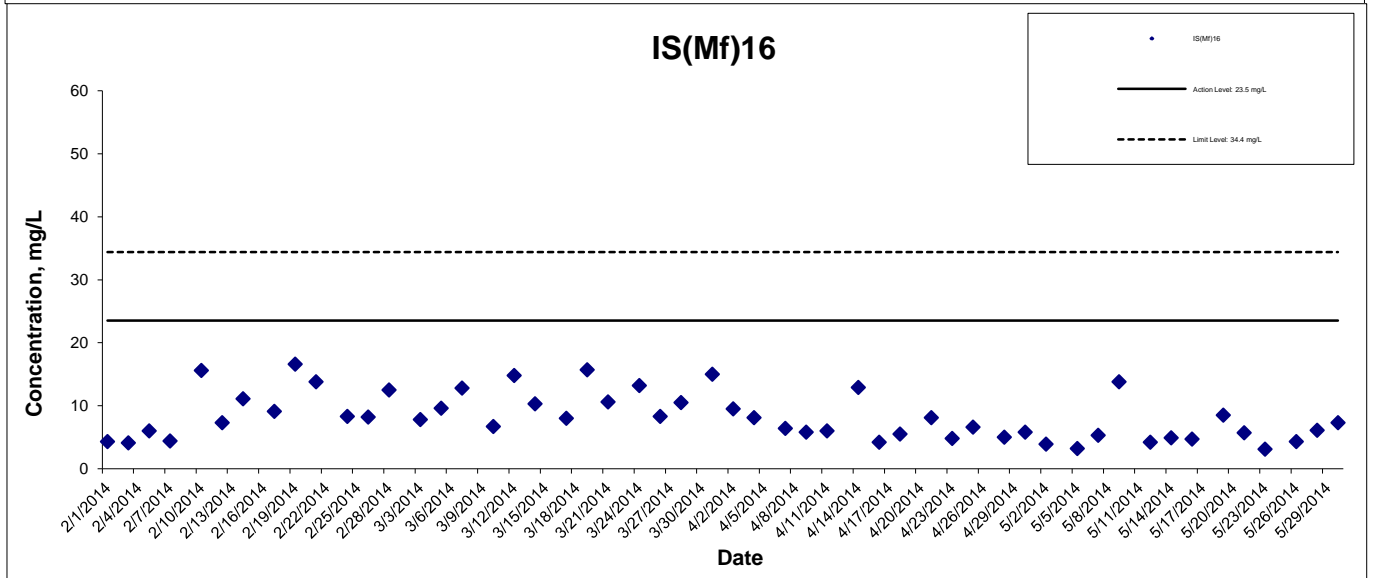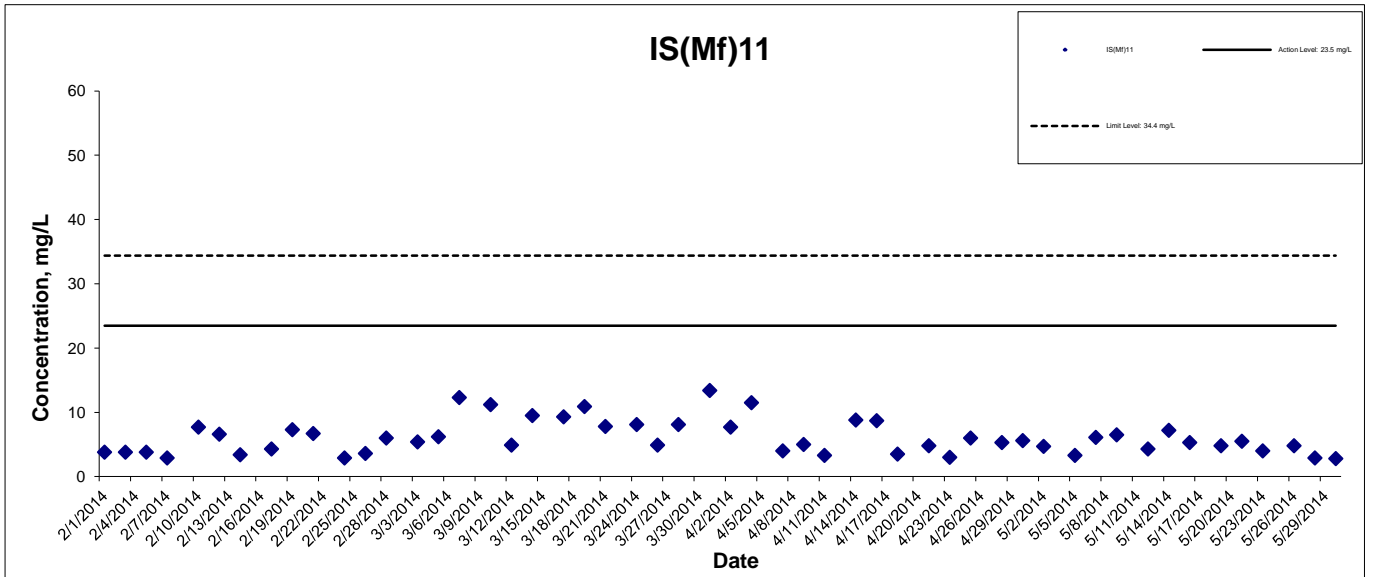


This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

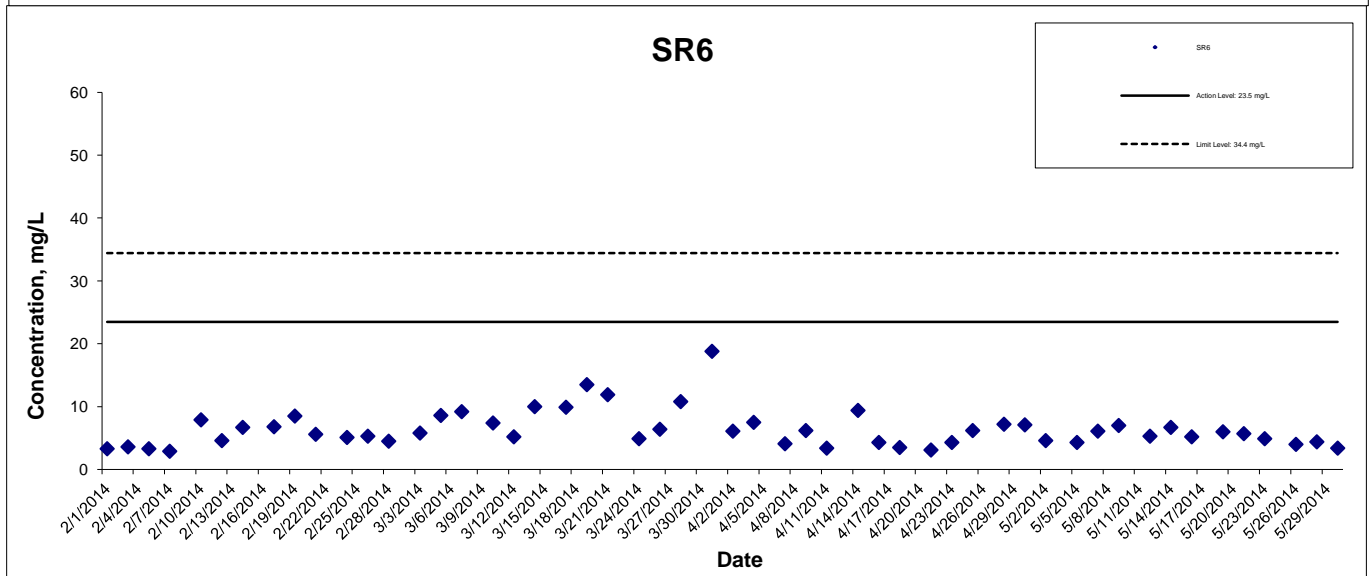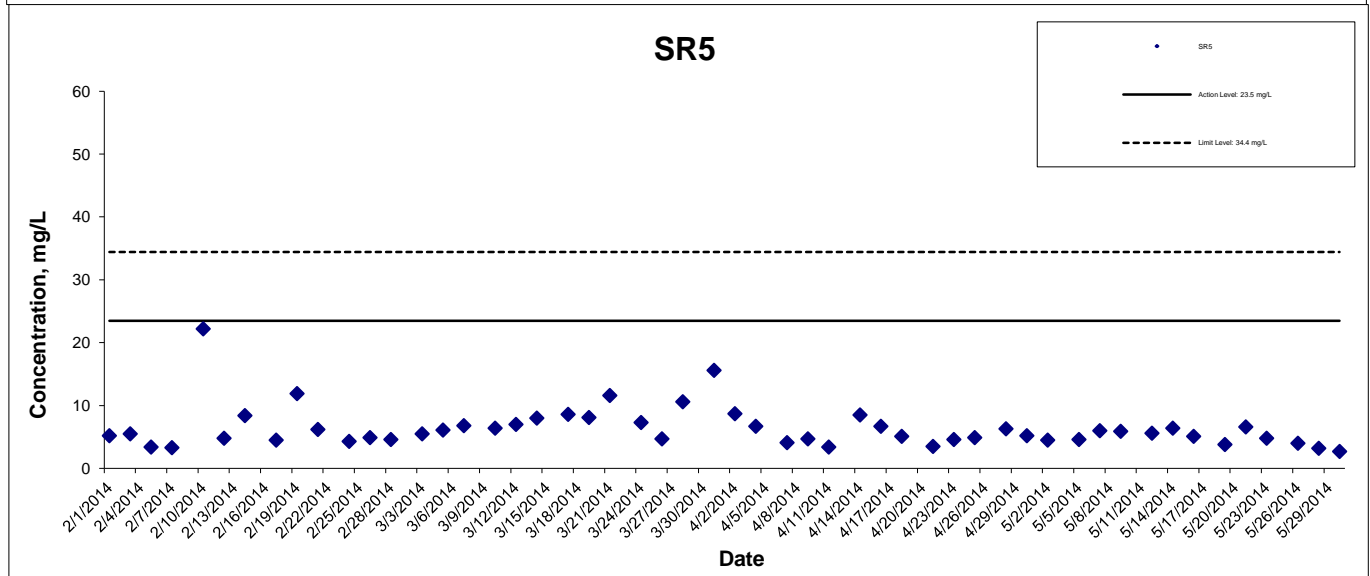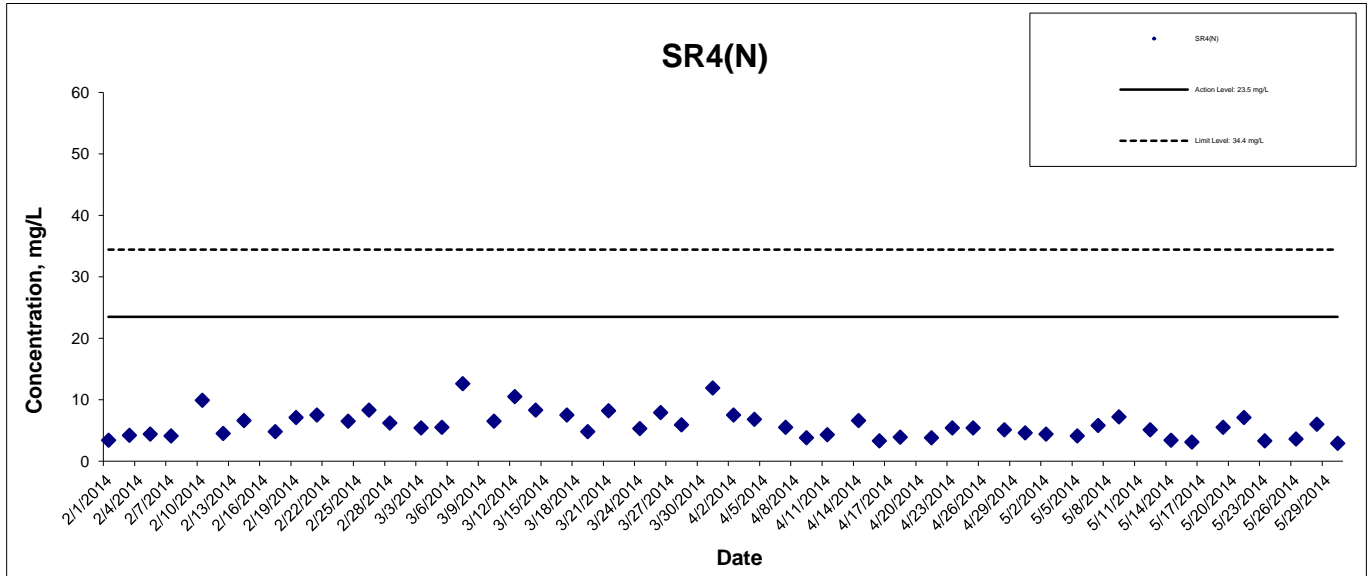




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Ebb Tide

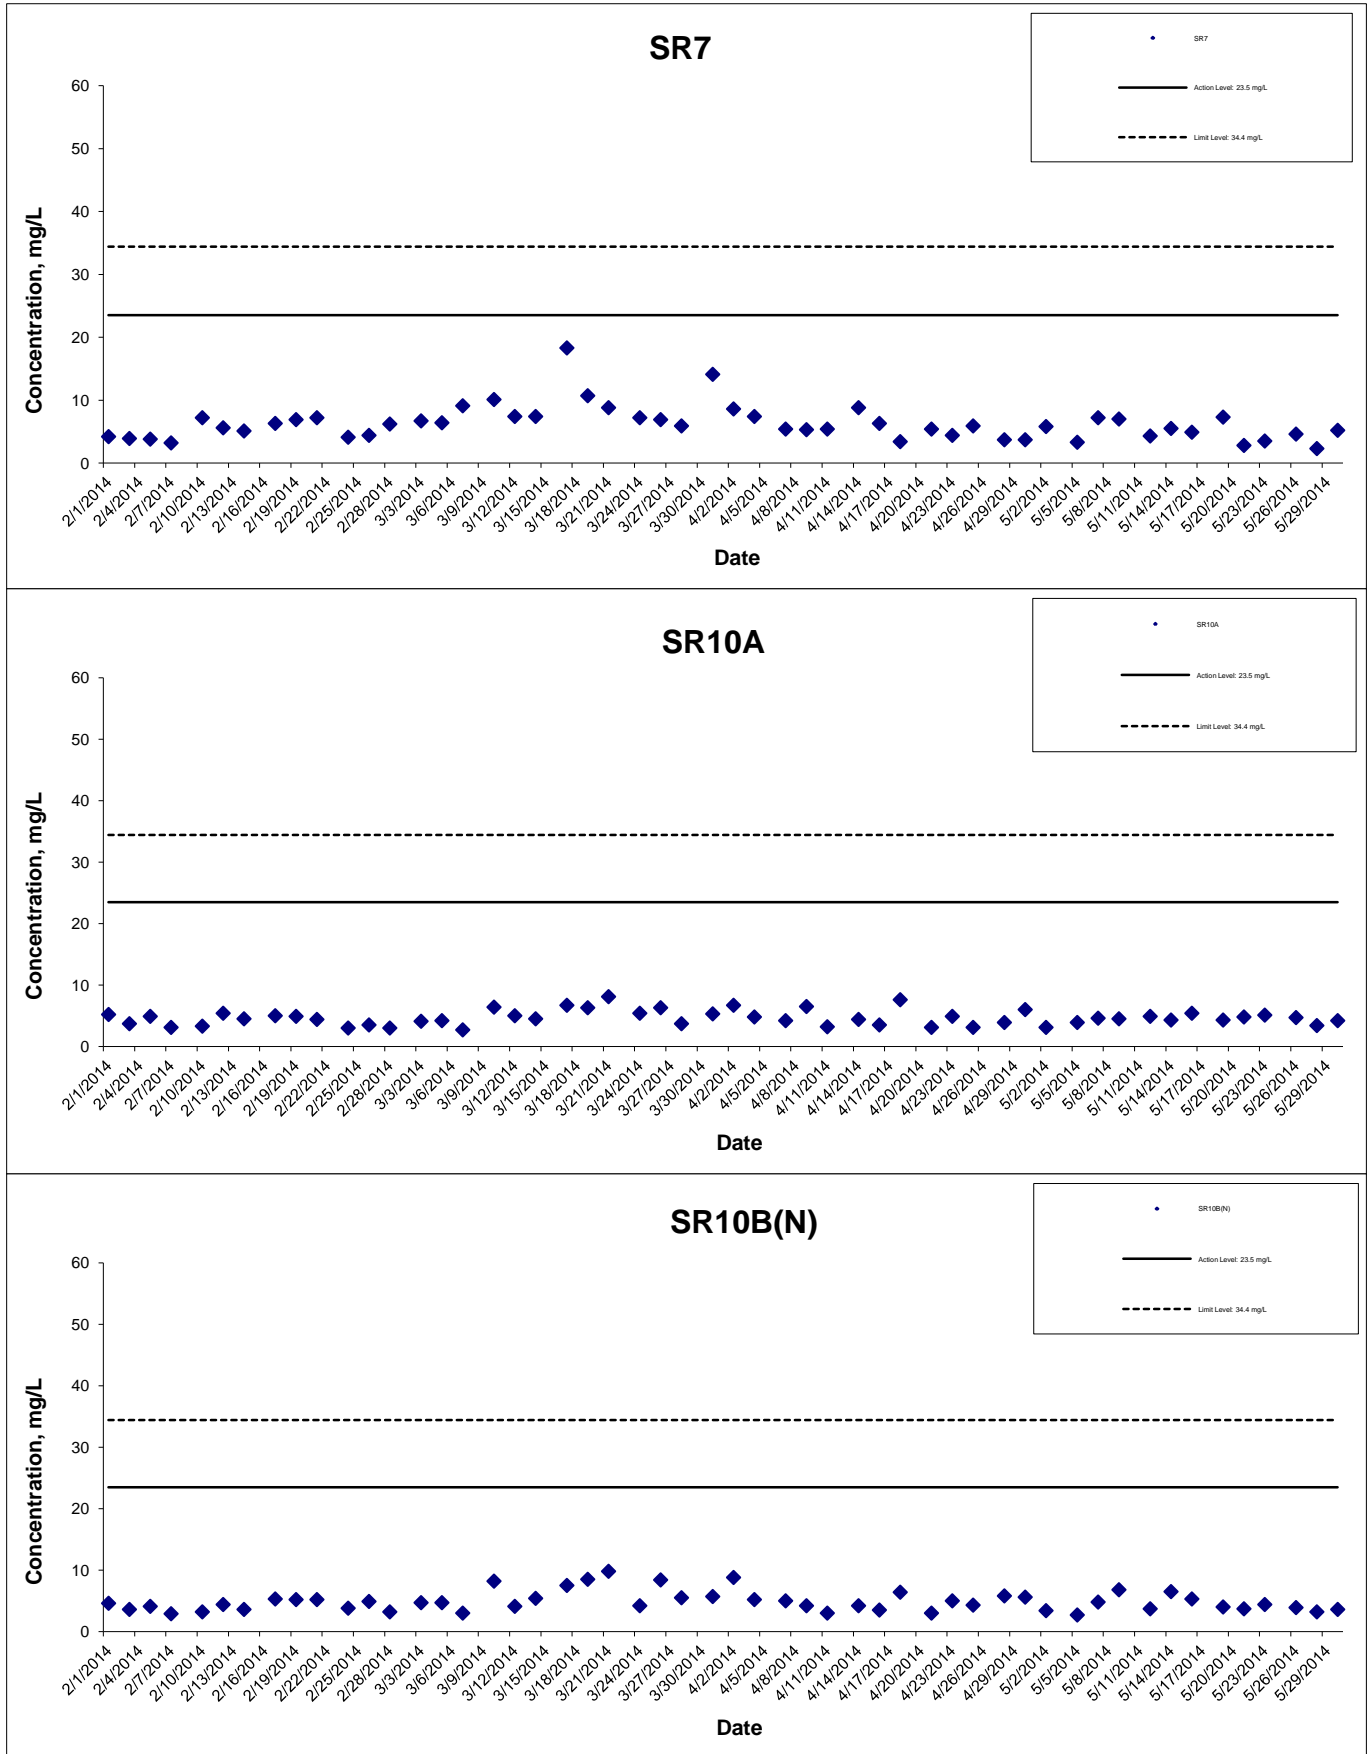




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Flood Tide

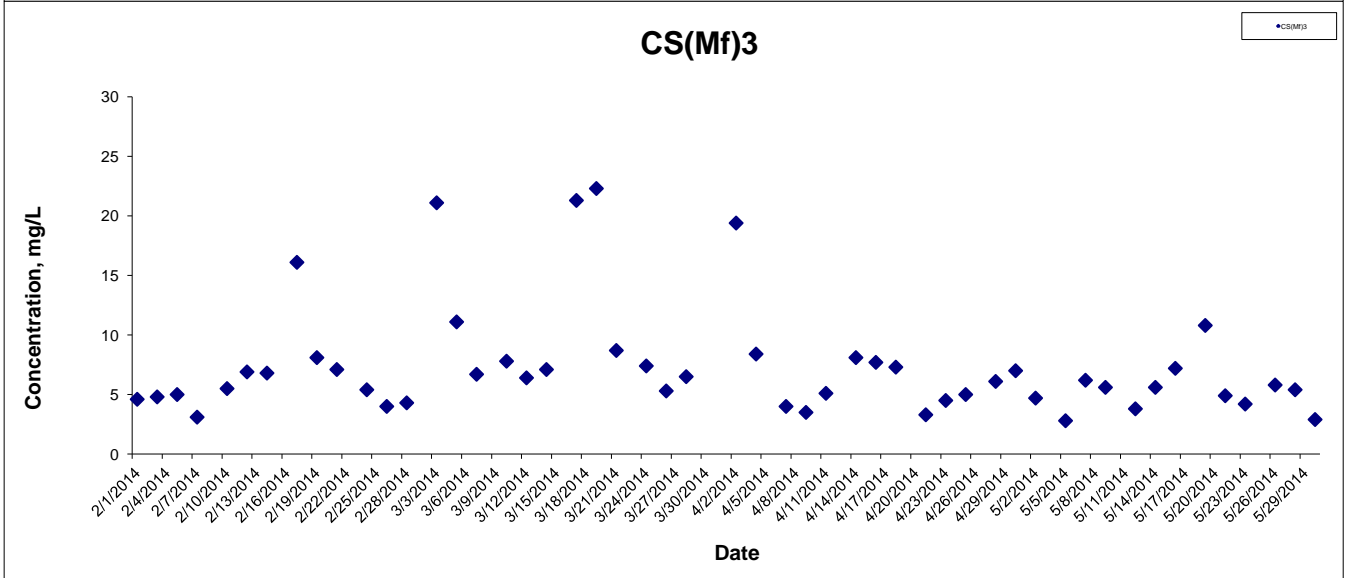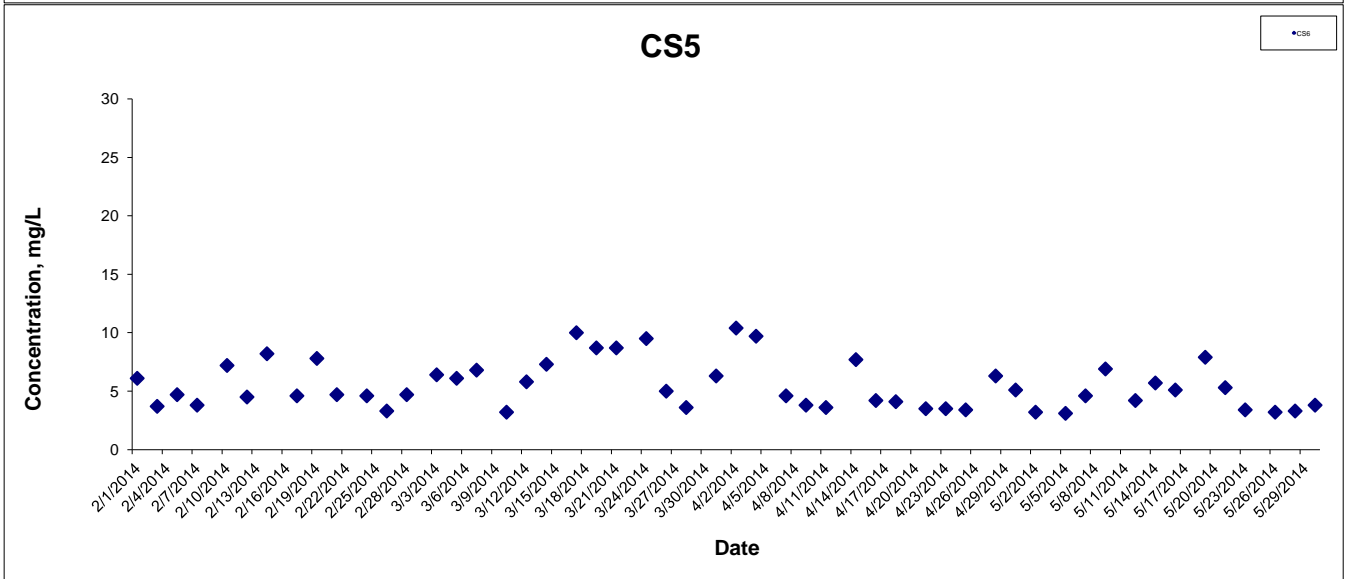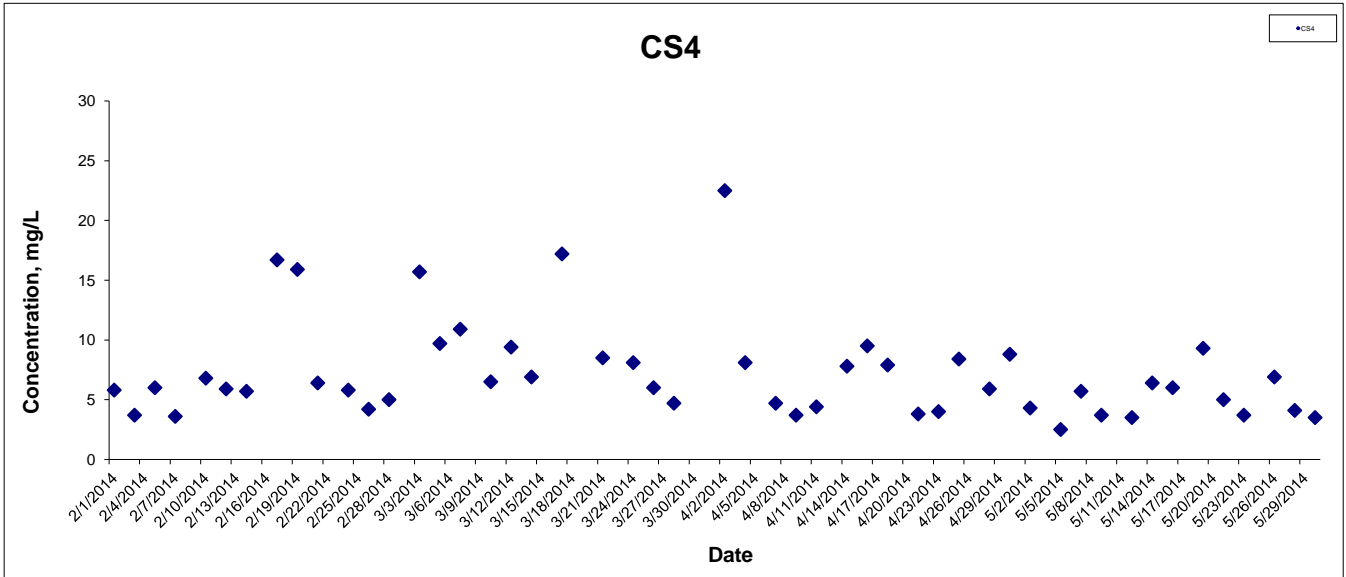

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Suspended Solids at Mid-Flood Tide

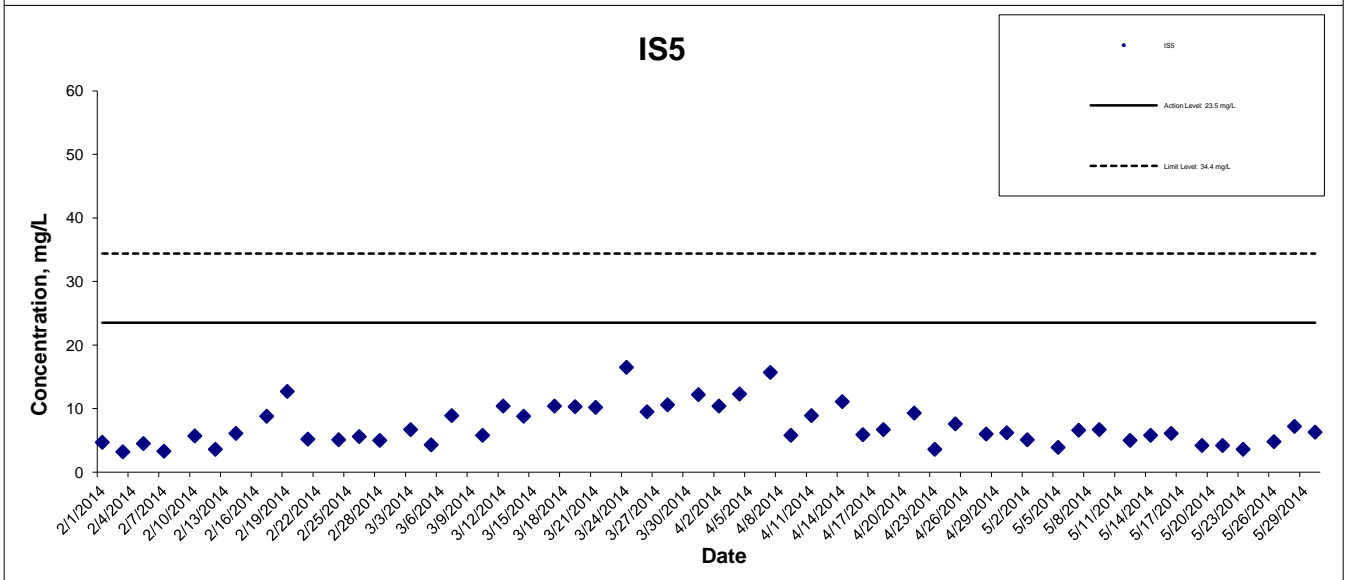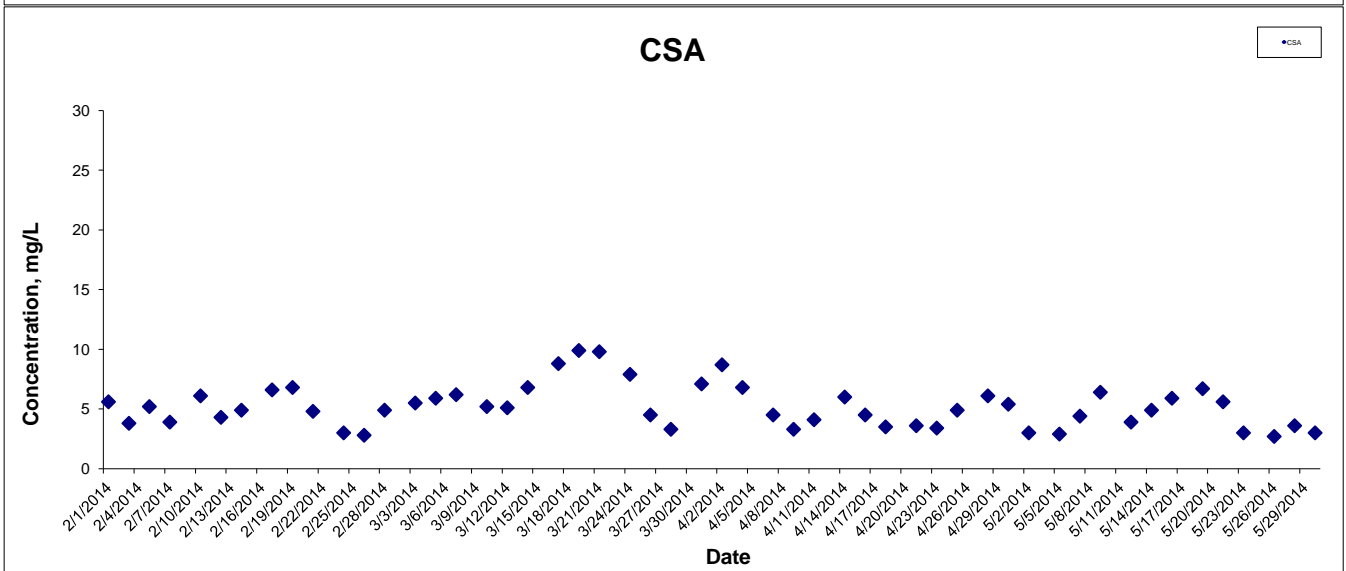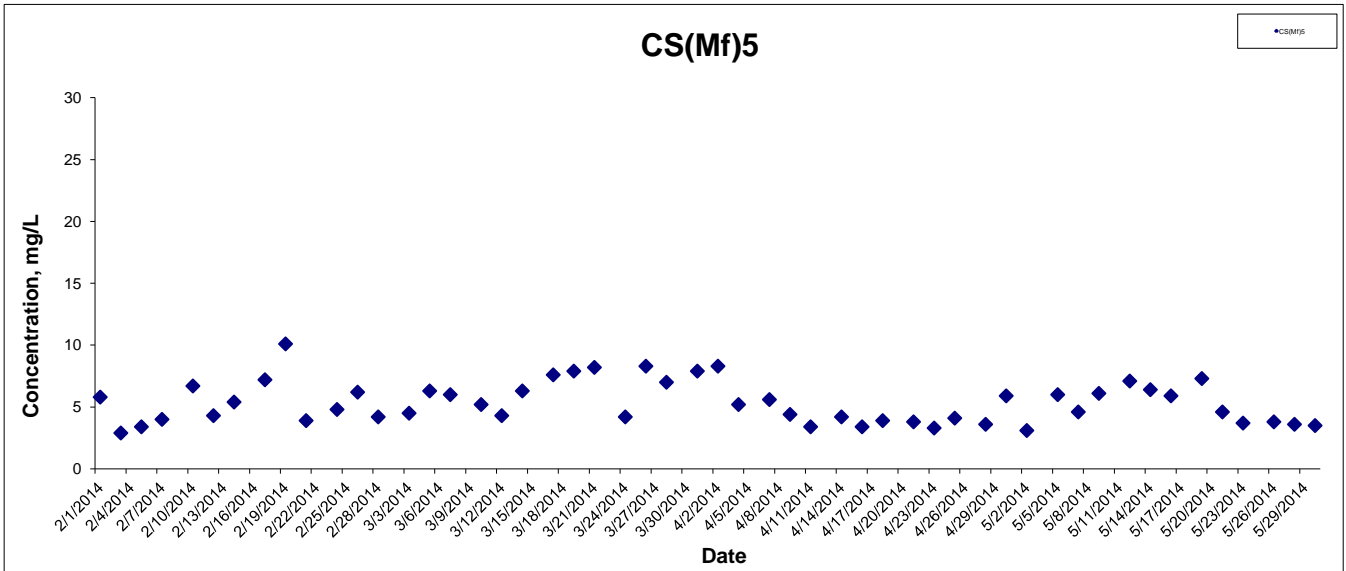

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE

HONG KONG BOUNDARY CROSSING FACILITIES

- RECLAMATION WORKS

**Graphical Presentation of Impact Water Quality
Monitoring Results**




Project No.: 60249820

Date: June 2014

Appendix J

Suspended Solids at Mid-Flood Tide

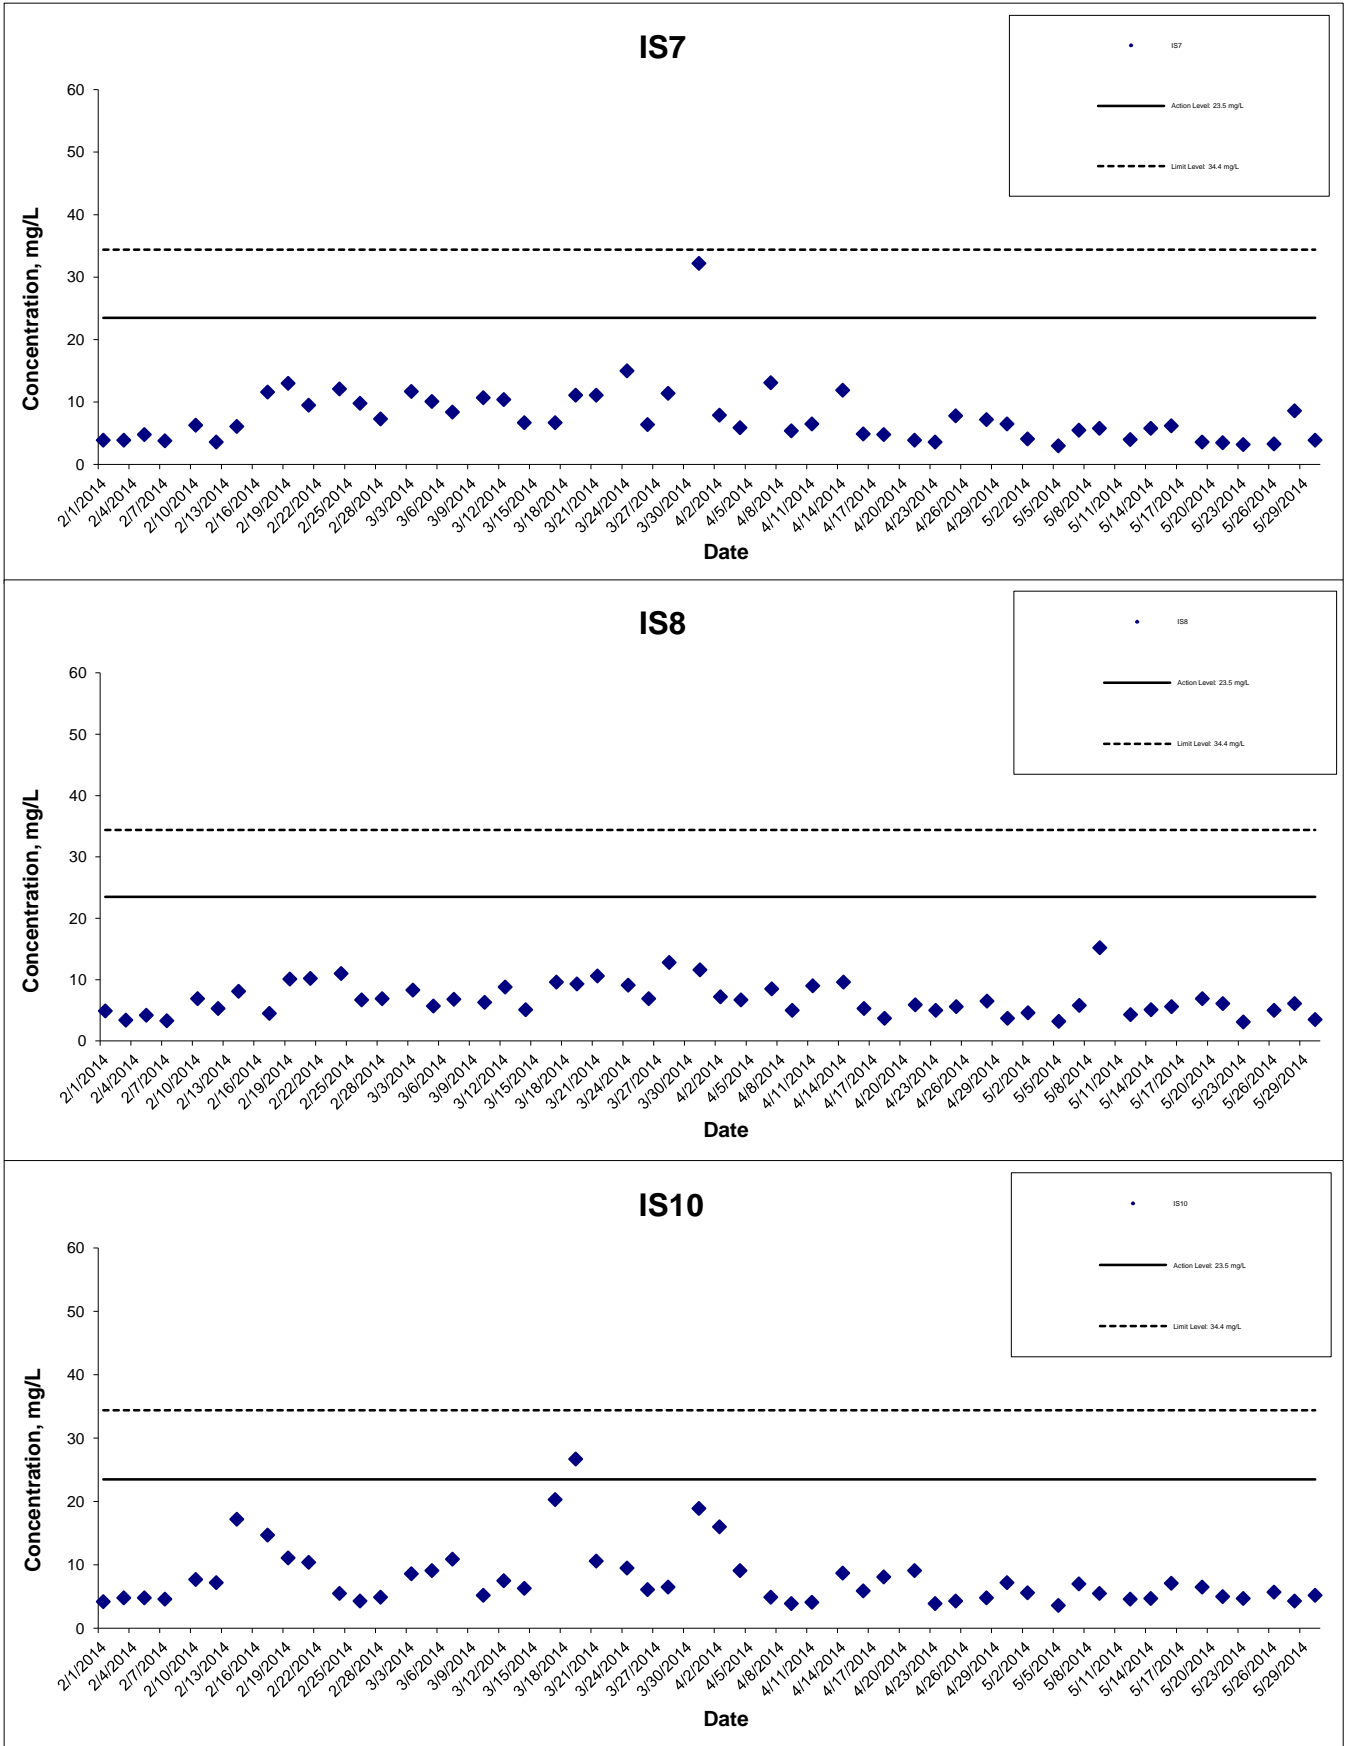

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE




HONG KONG BOUNDARY CROSSING FACILITIES

- RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
Monitoring Results



Suspended Solids at Mid-Flood Tide

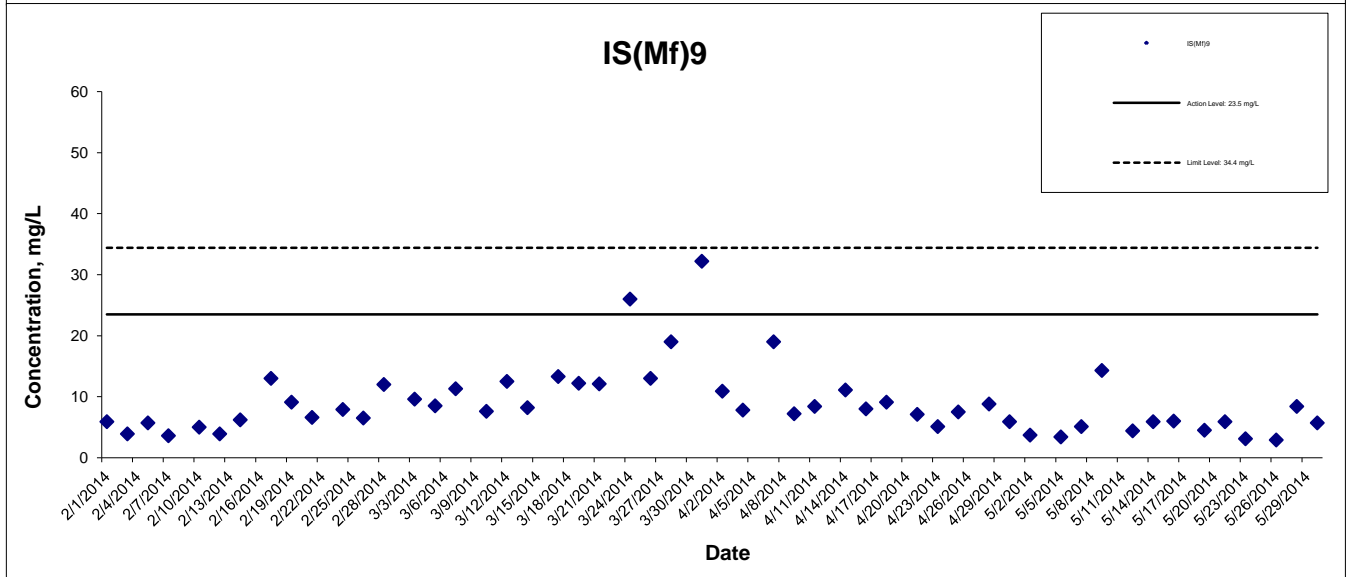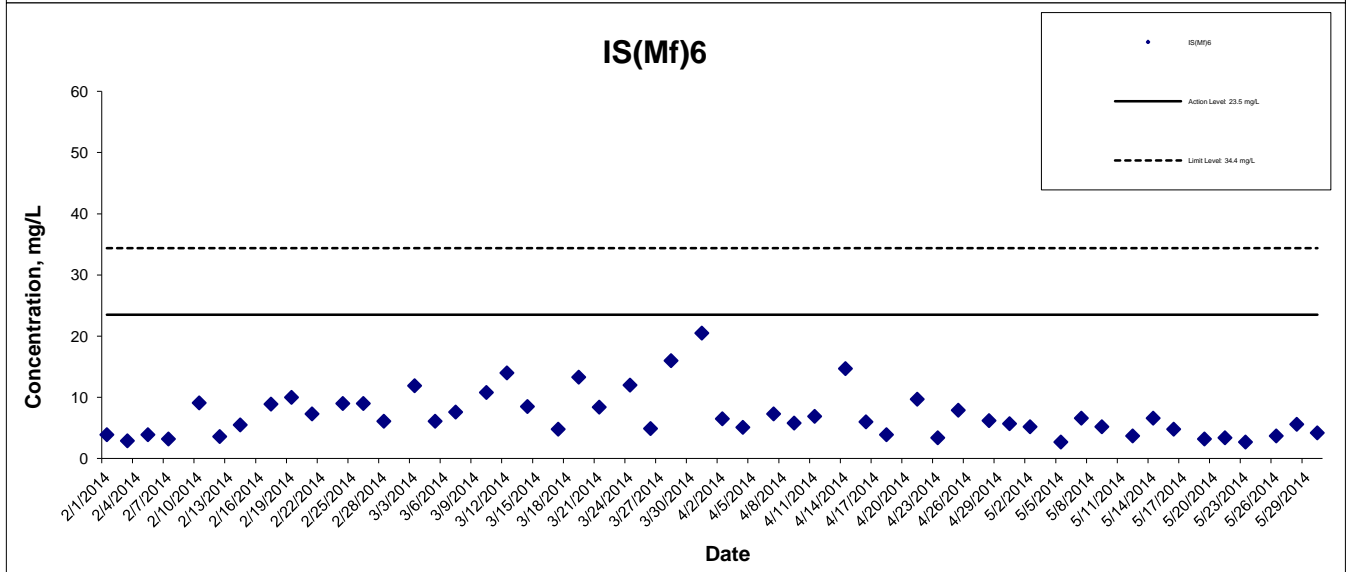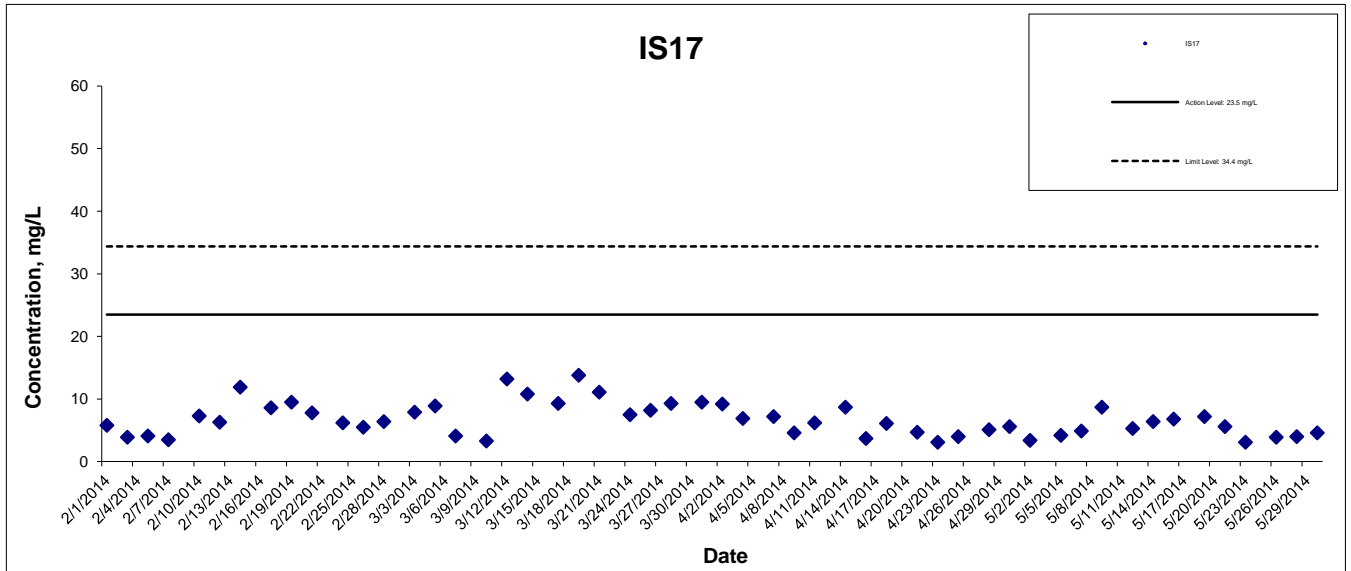

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE




HONG KONG BOUNDARY CROSSING FACILITIES

- RECLAMATION WORKS

**Graphical Presentation of Impact Water Quality
Monitoring Results**



Suspended Solids at Mid-Flood Tide

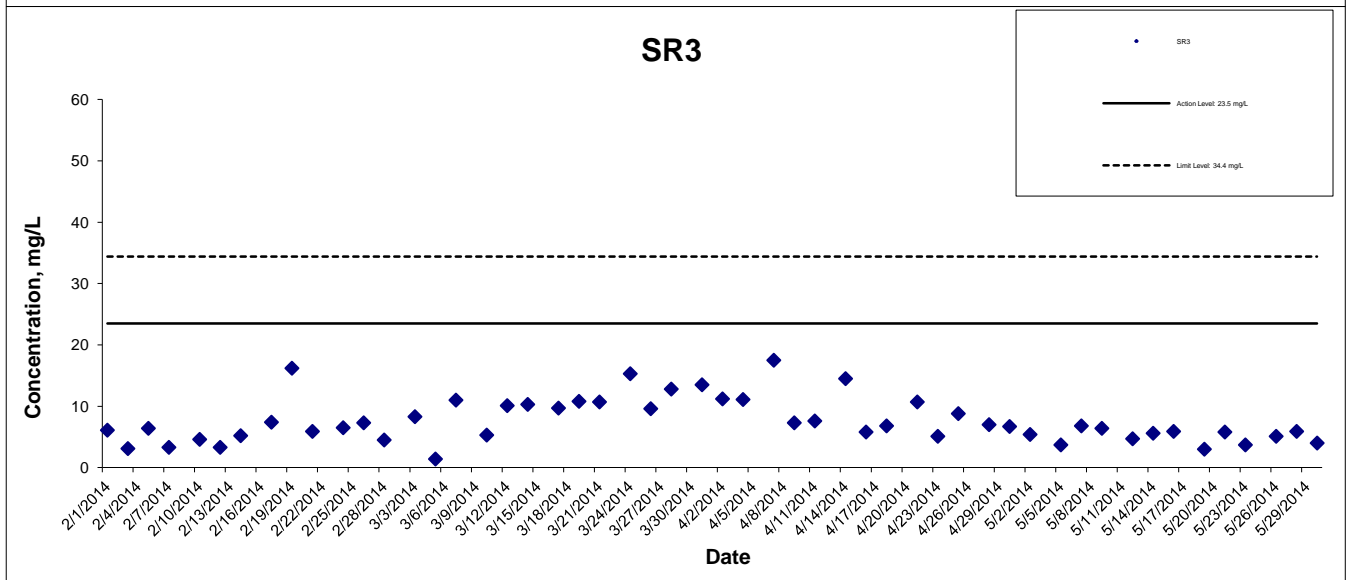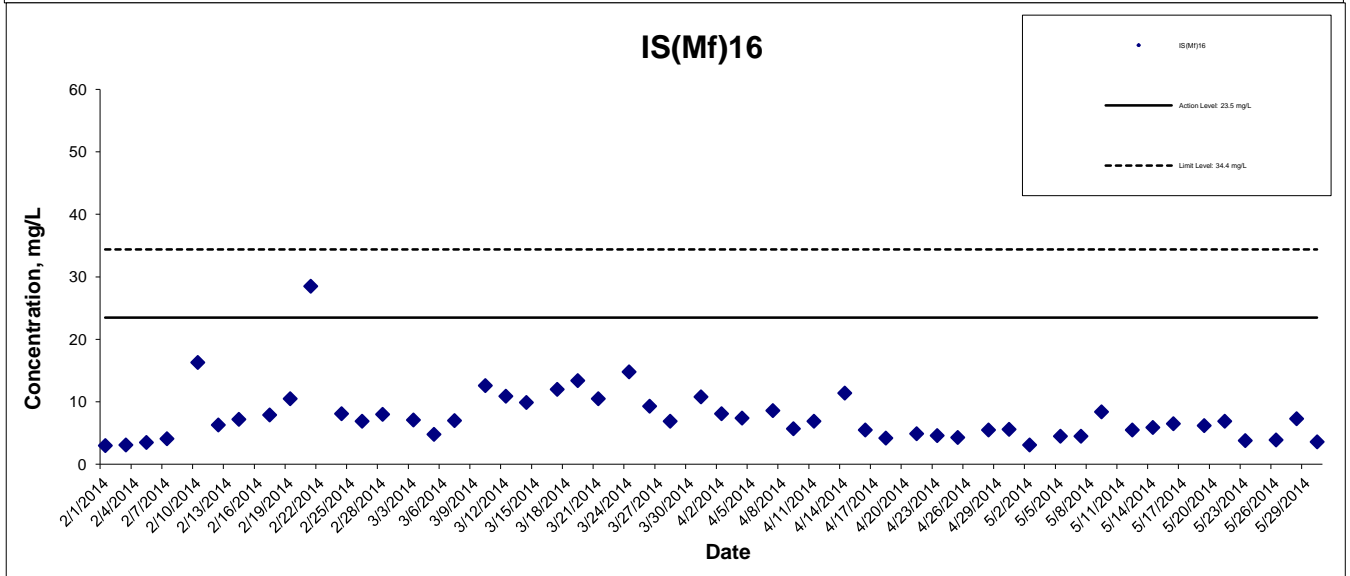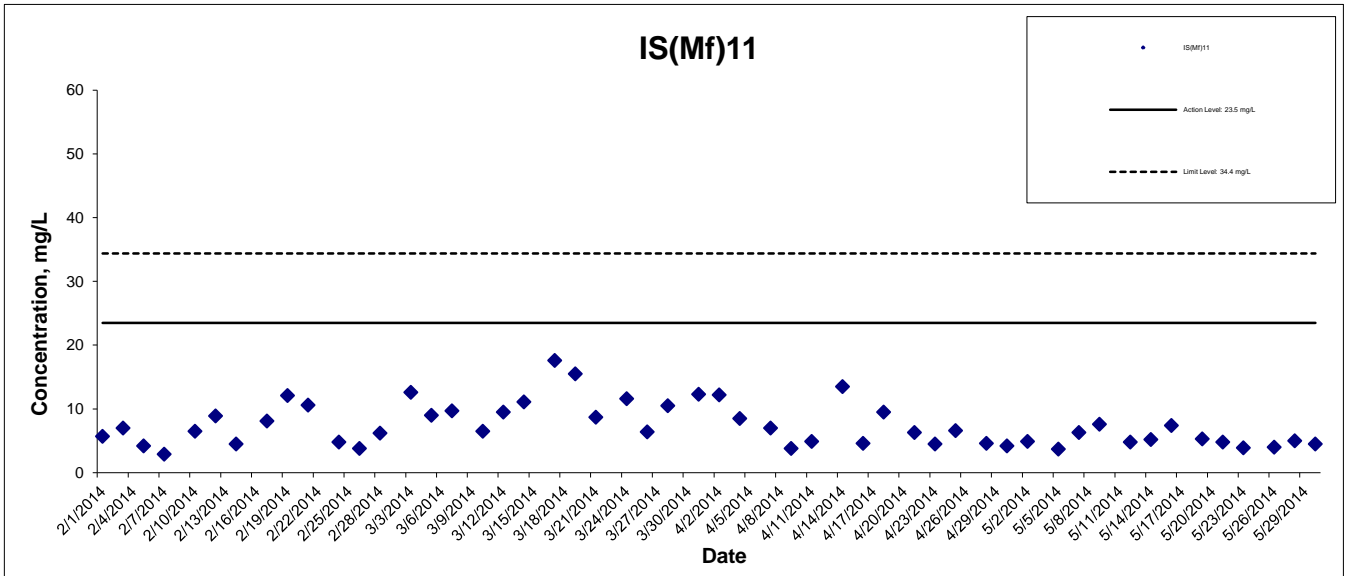

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE




HONG KONG BOUNDARY CROSSING FACILITIES

- RECLAMATION WORKS

**Graphical Presentation of Impact Water Quality
Monitoring Results**






Suspended Solids at Mid-Flood Tide

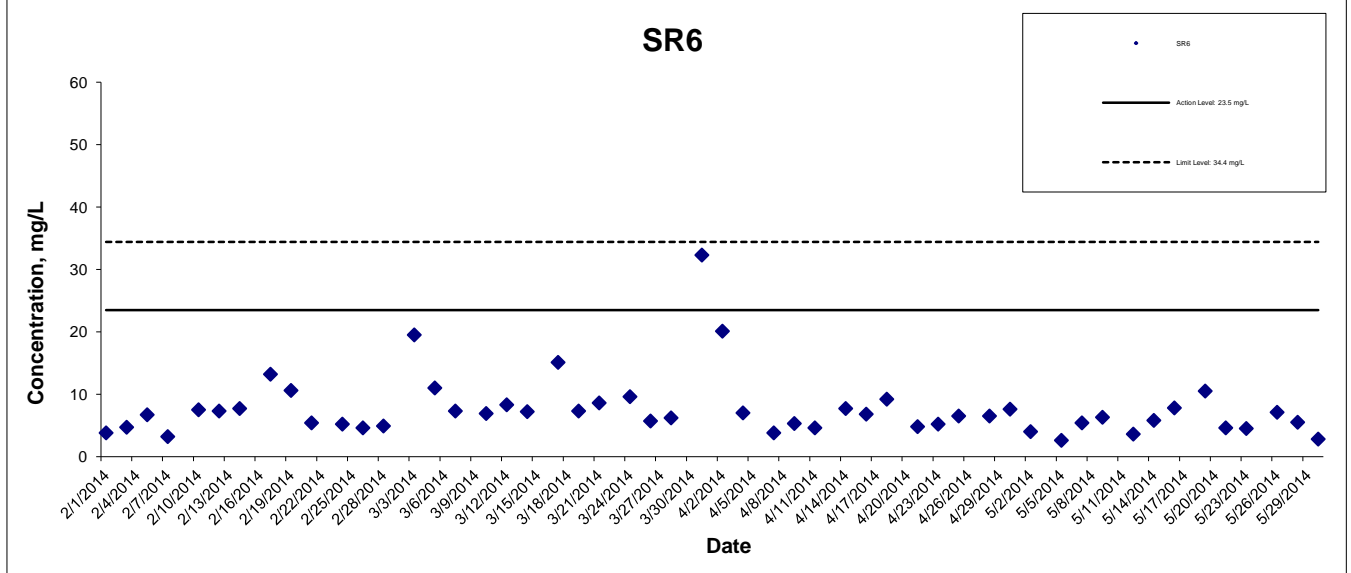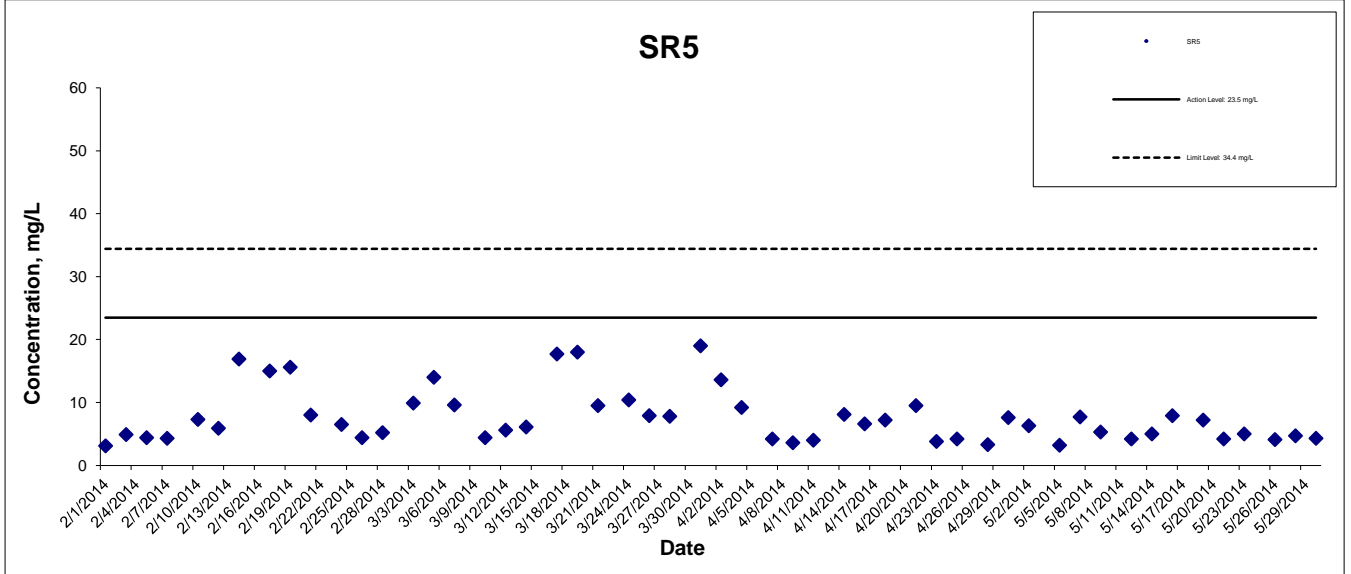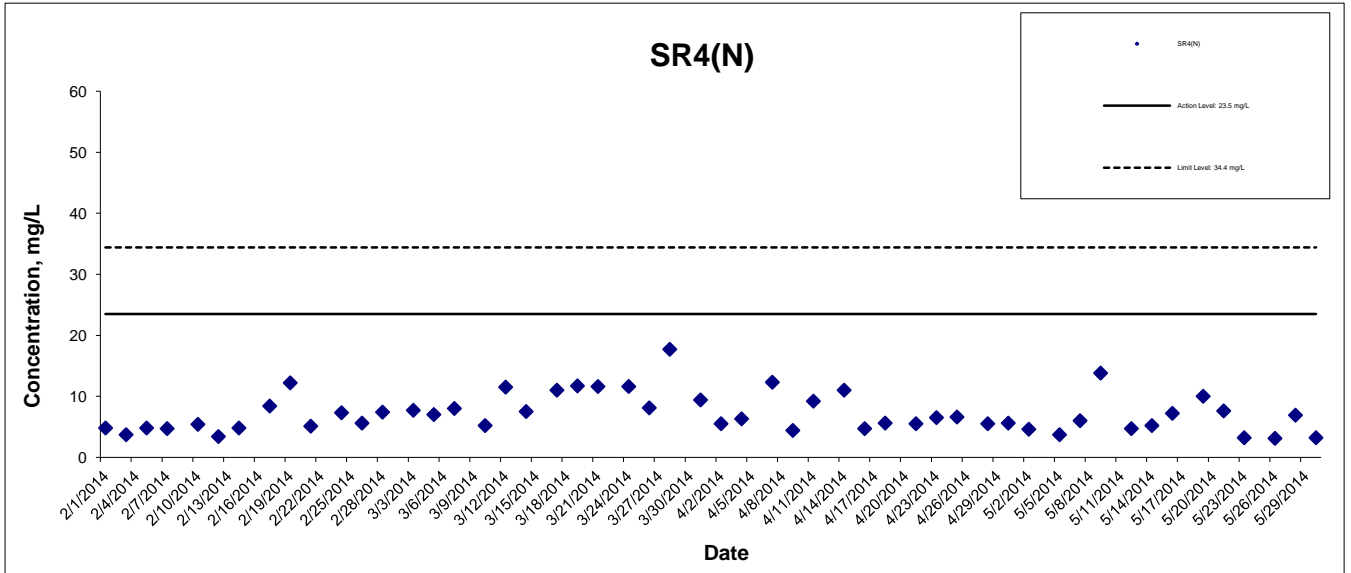

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.



Suspended Solids at Mid-Flood Tide

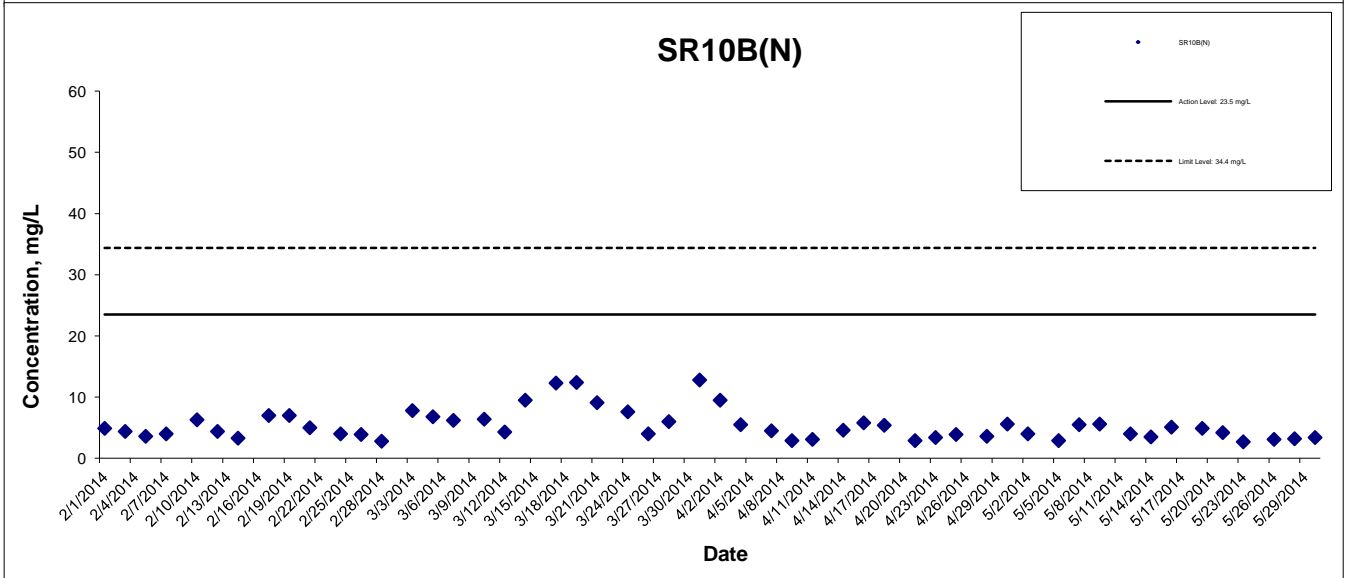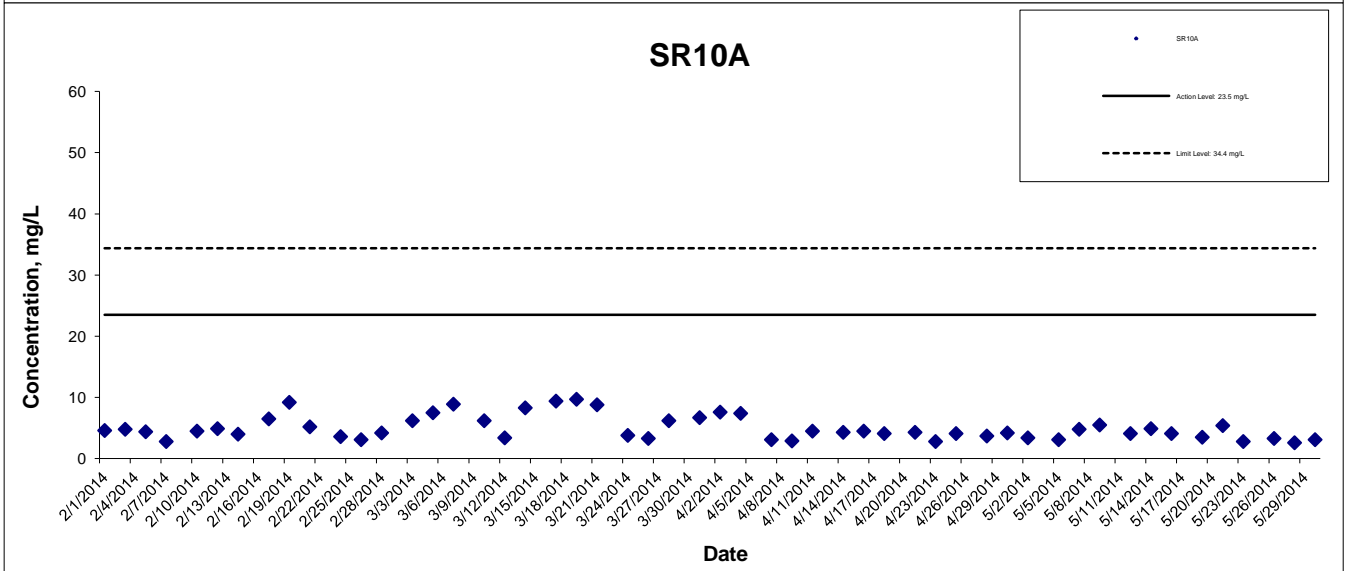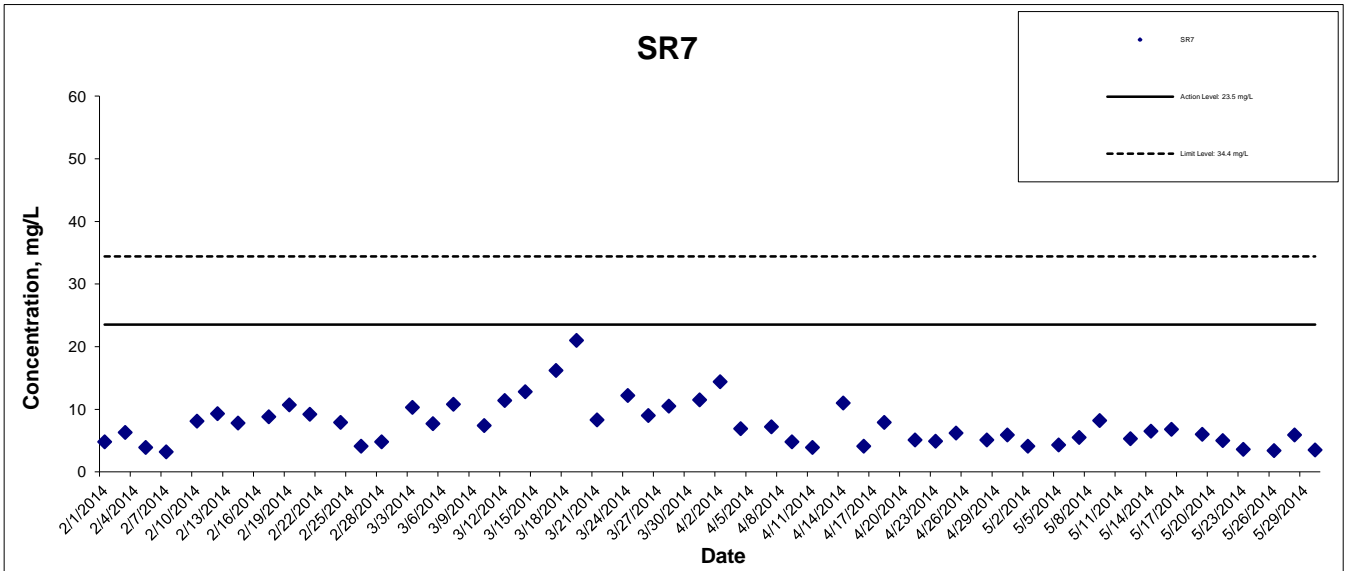

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE

HONG KONG BOUNDARY CROSSING FACILITIES

- RECLAMATION WORKS

**Graphical Presentation of Impact Water Quality
Monitoring Results**






Project No.: 60249820

Date: June 2014




Appendix J

Turbidity at Mid-Ebb Tide

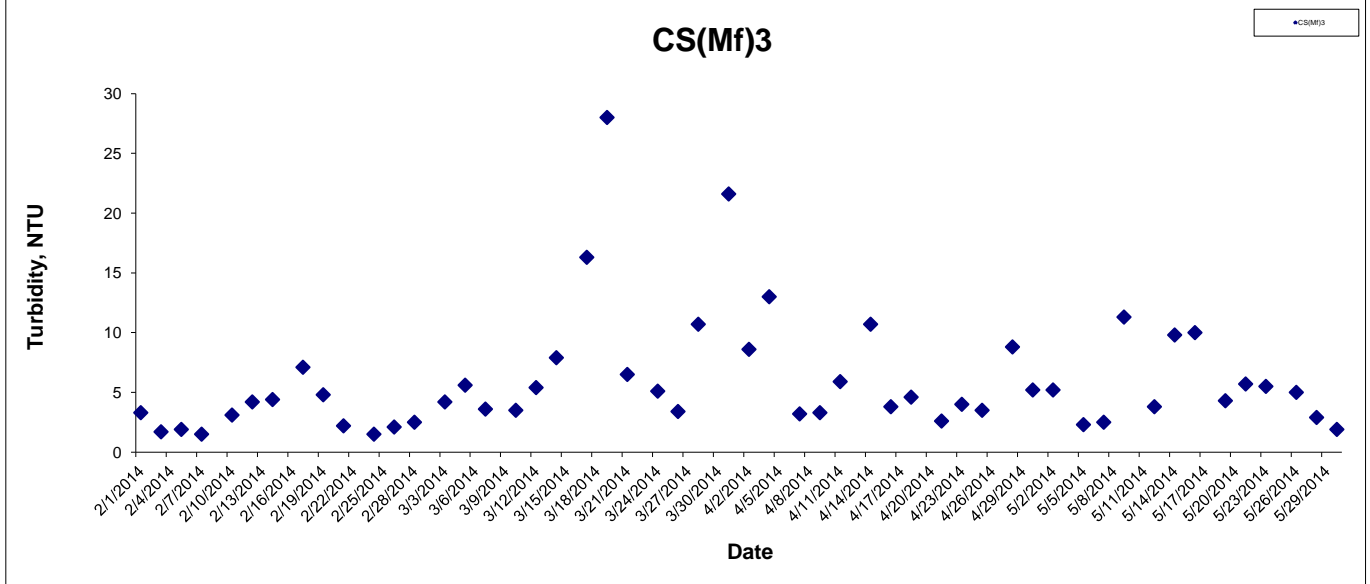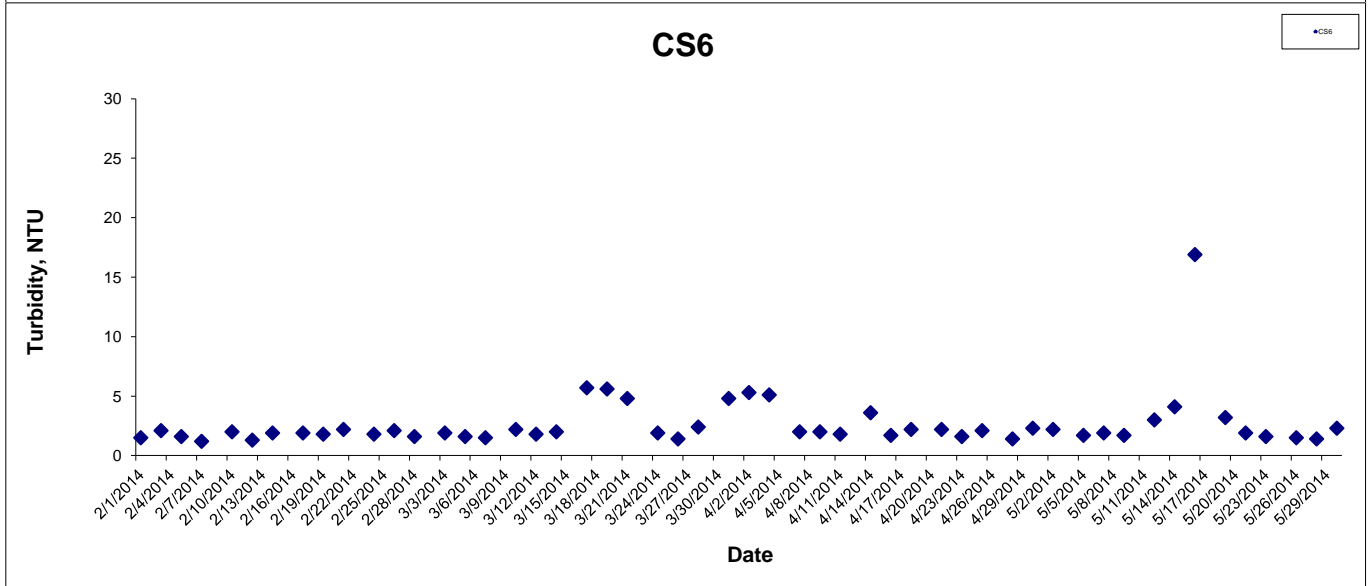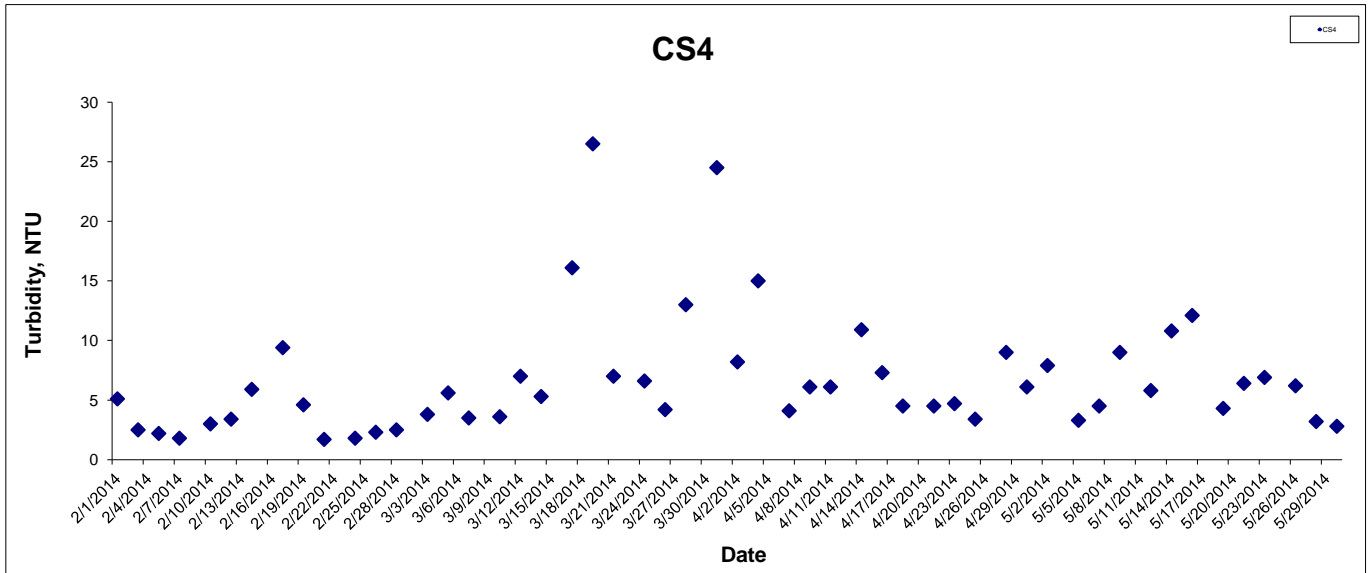




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Ebb Tide

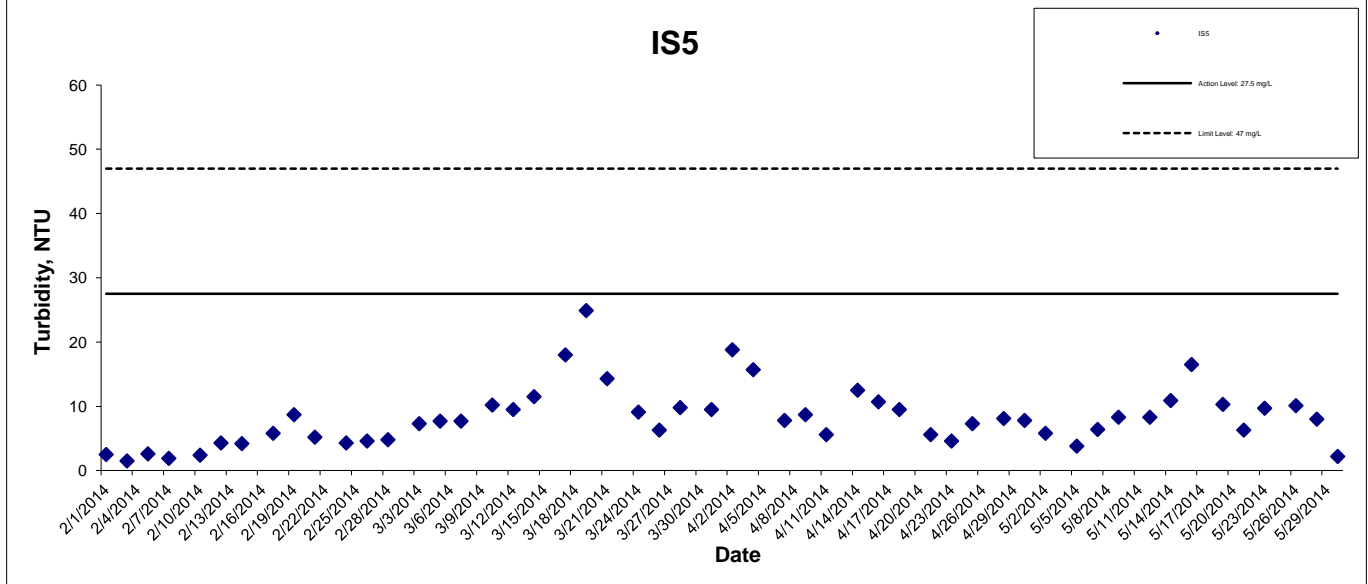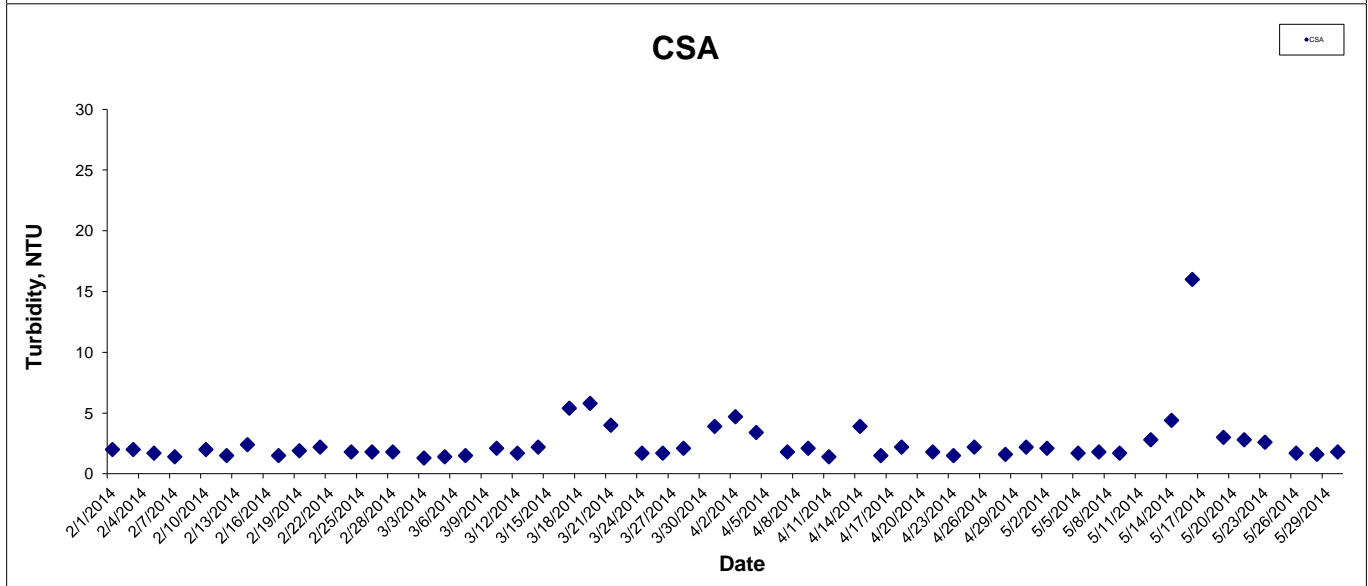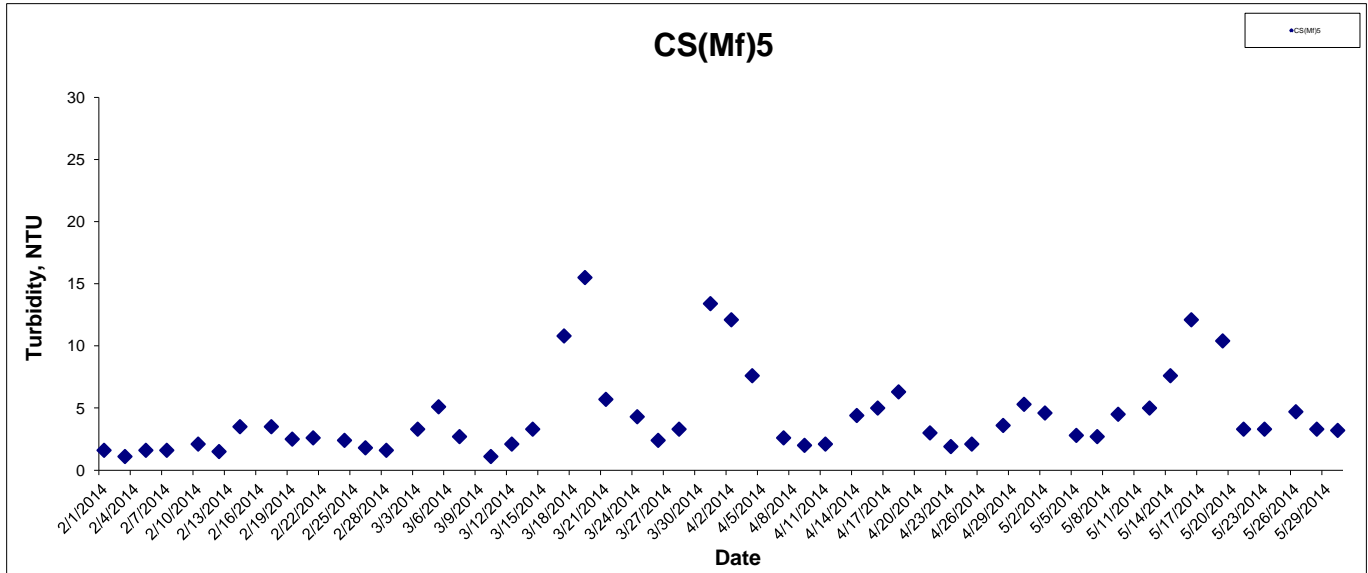


This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Ebb Tide

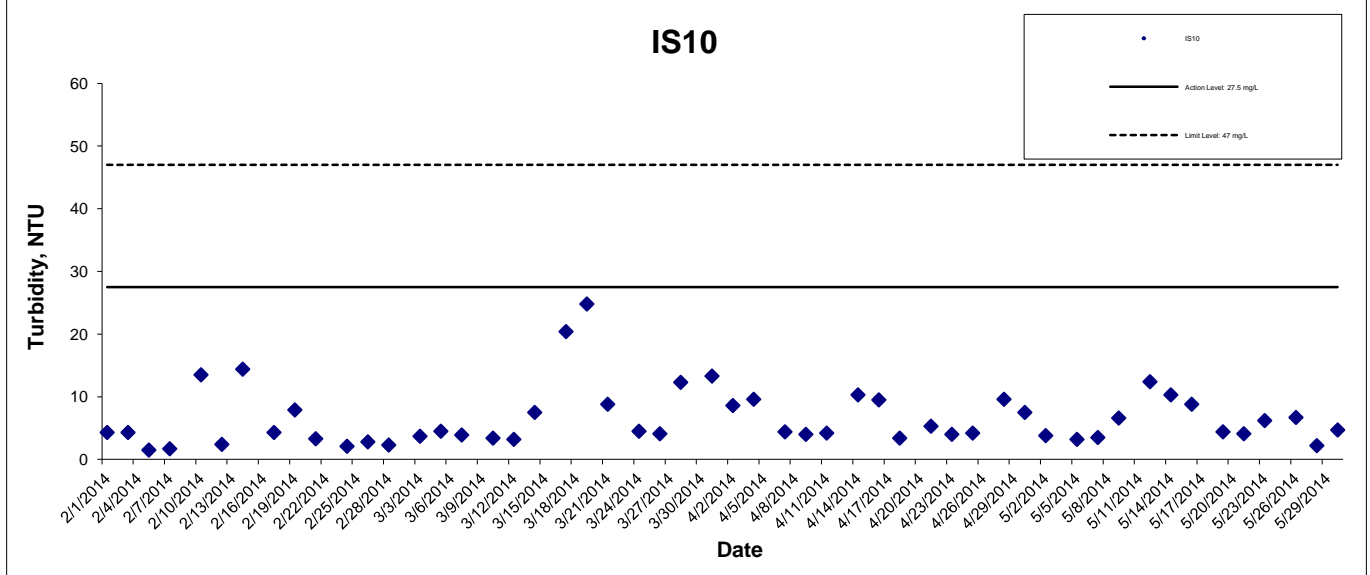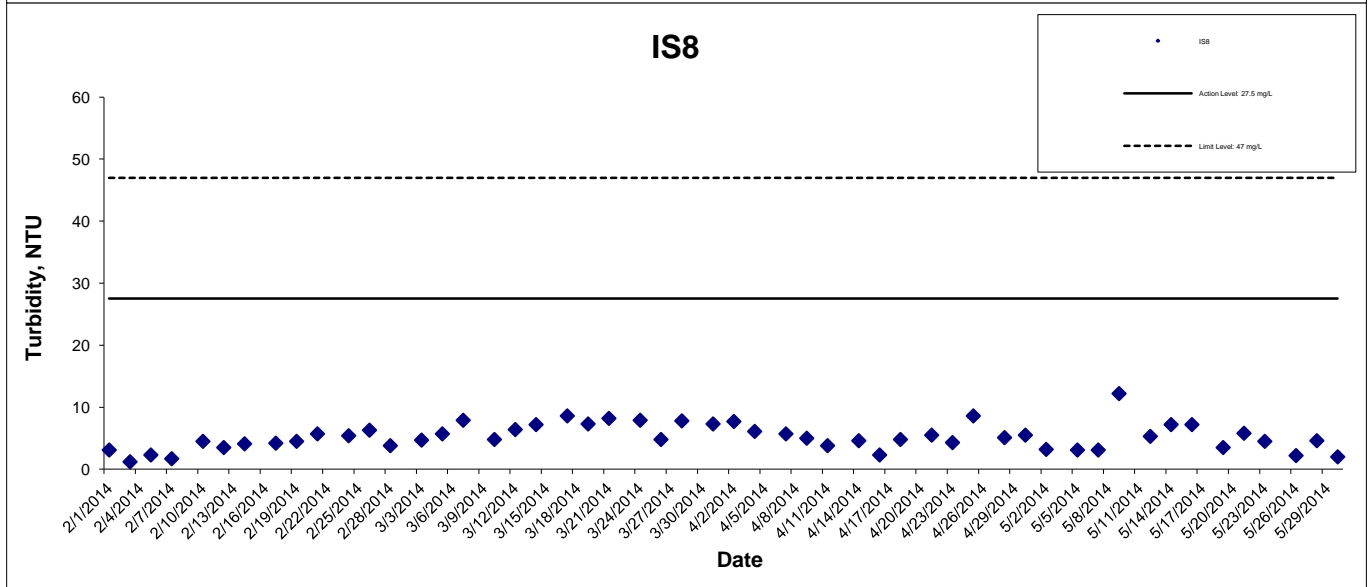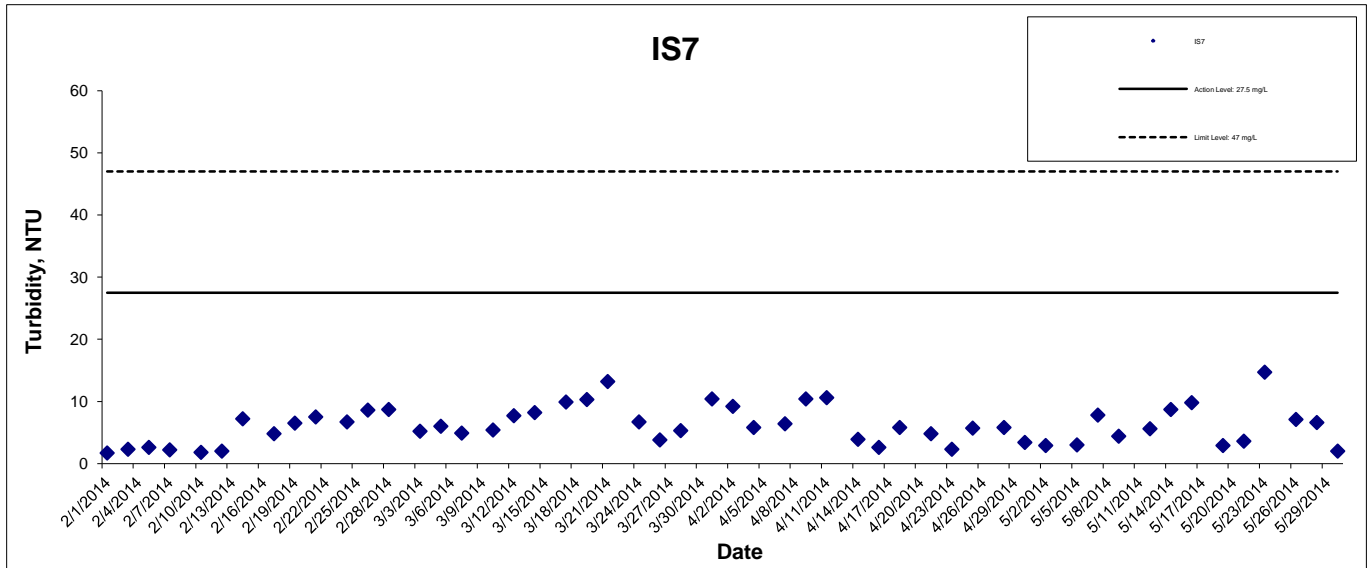




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Ebb Tide

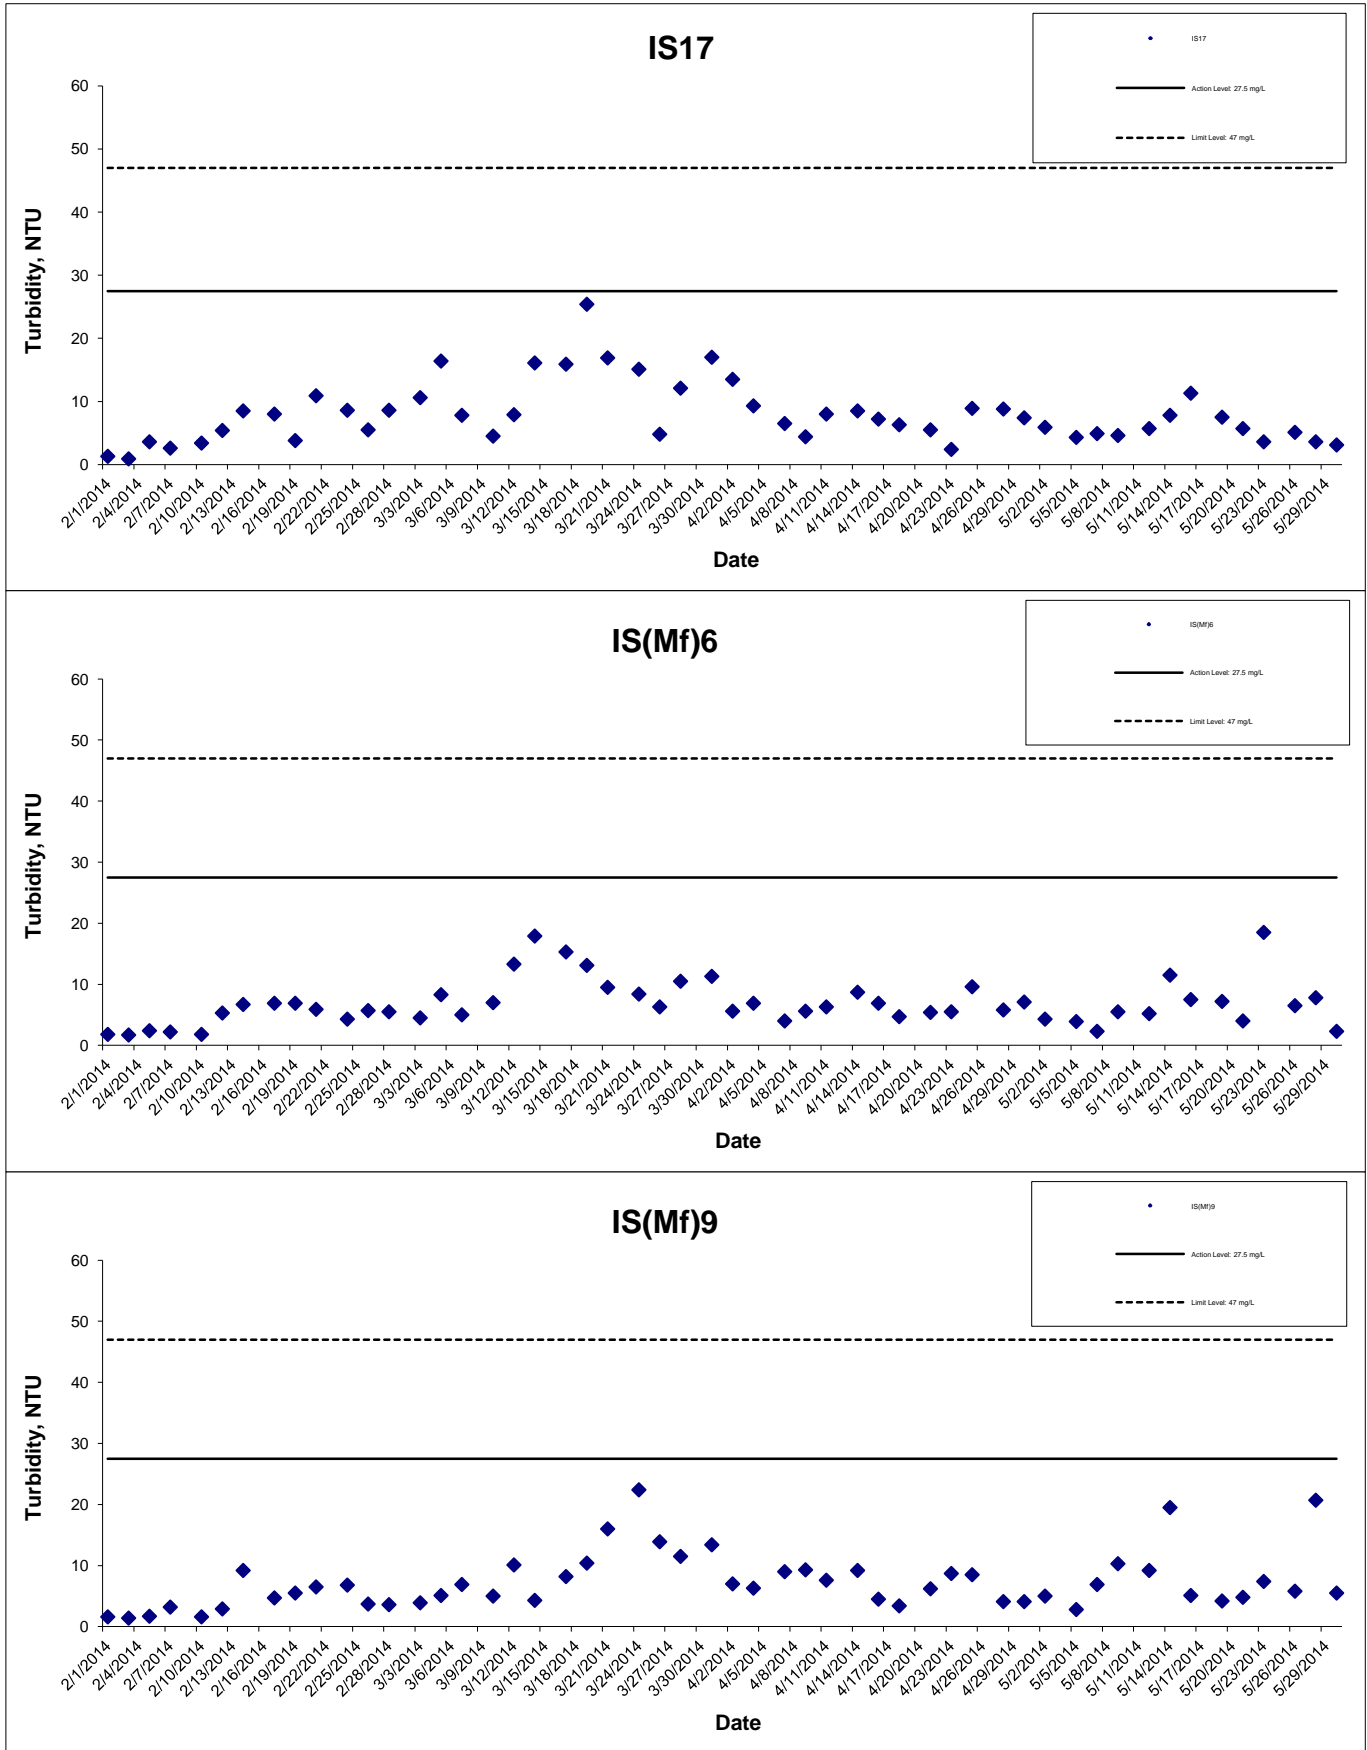

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Ebb Tide

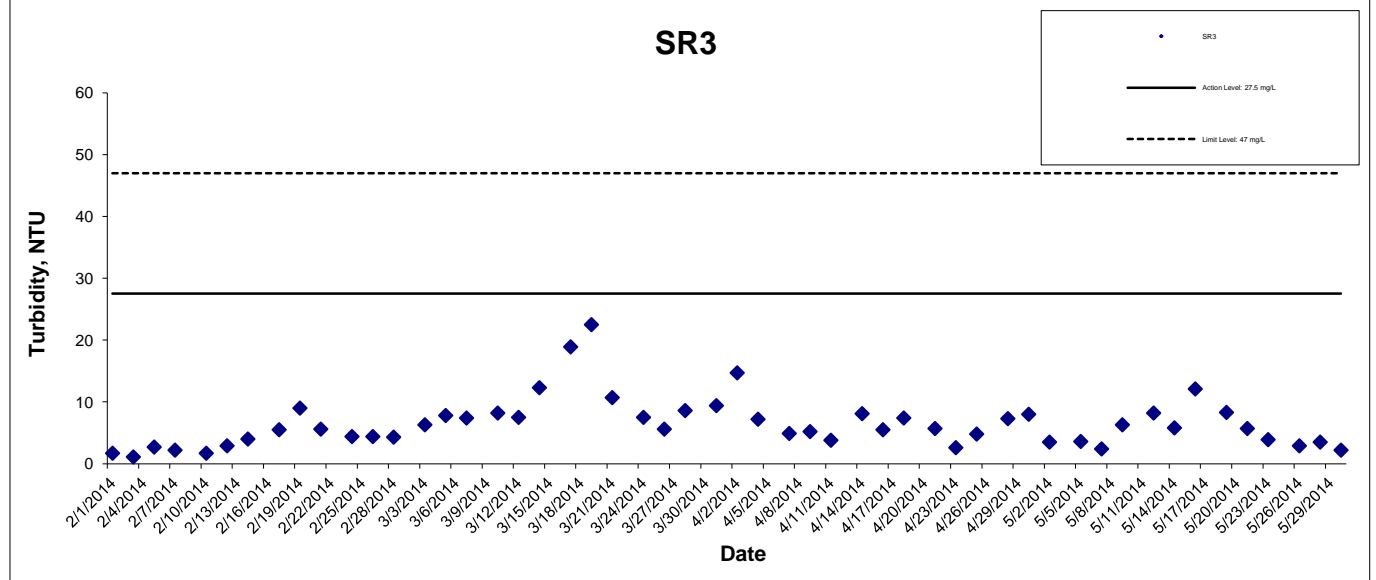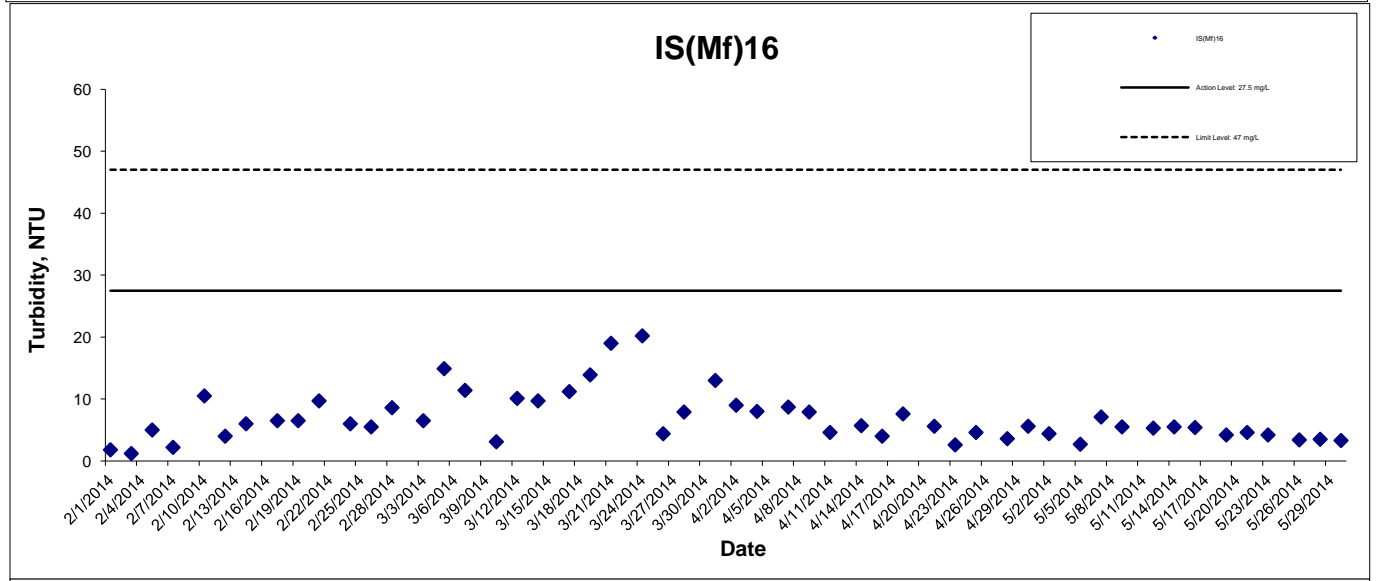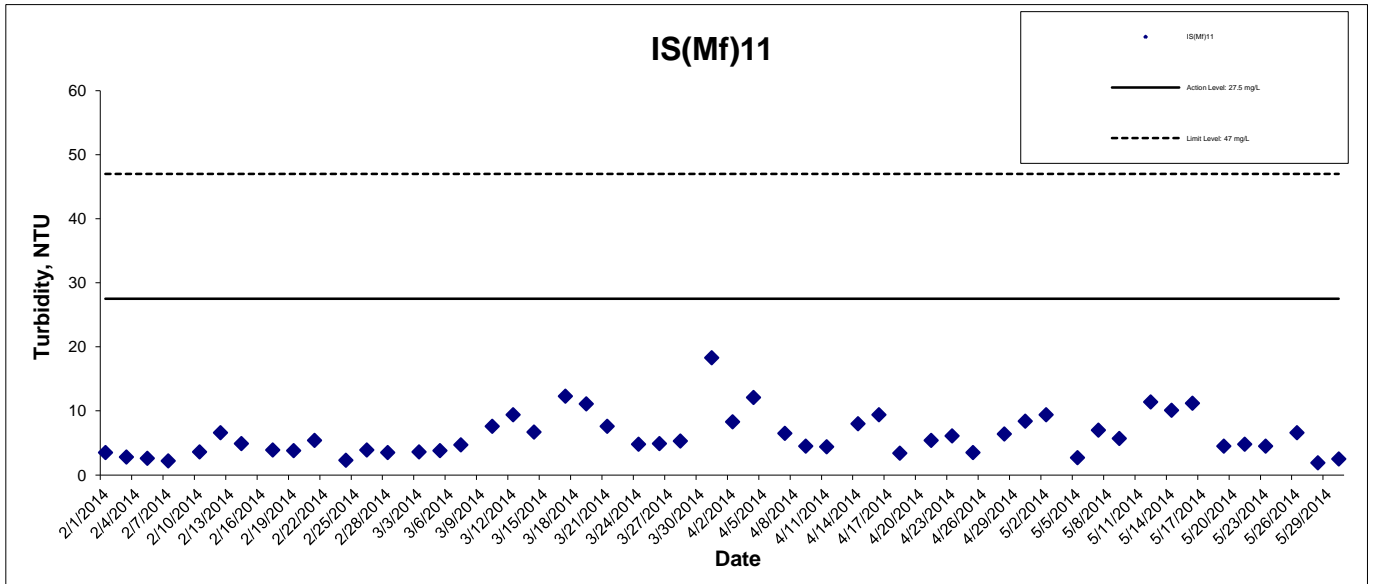




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
Monitoring Results




Turbidity at Mid-Ebb Tide

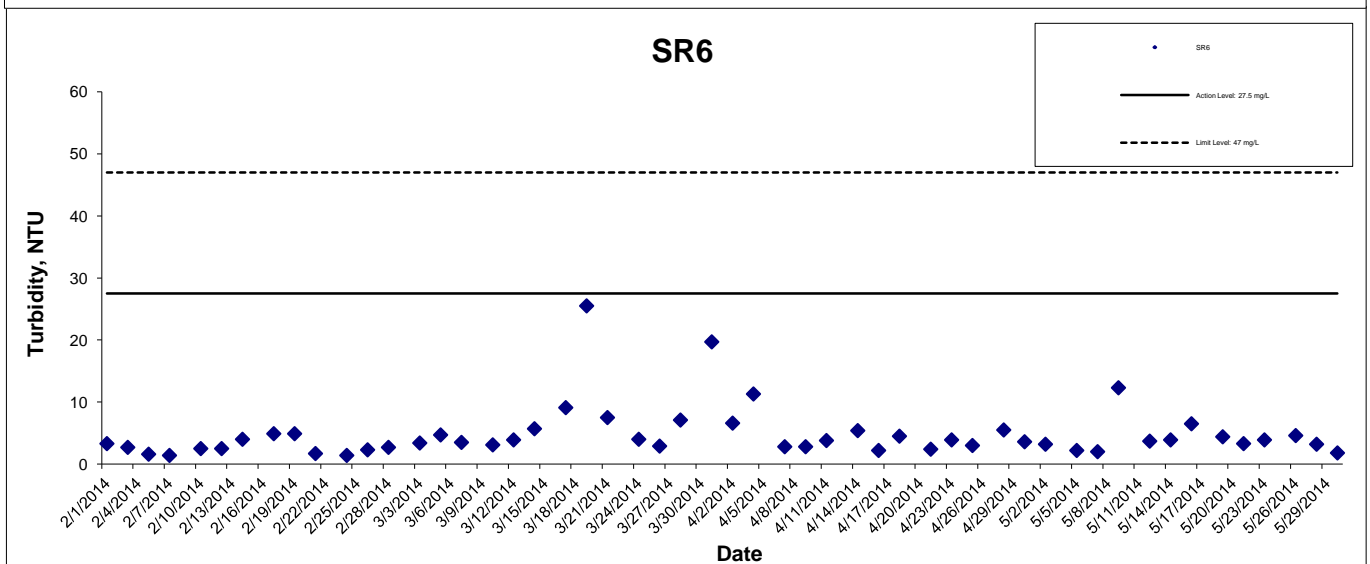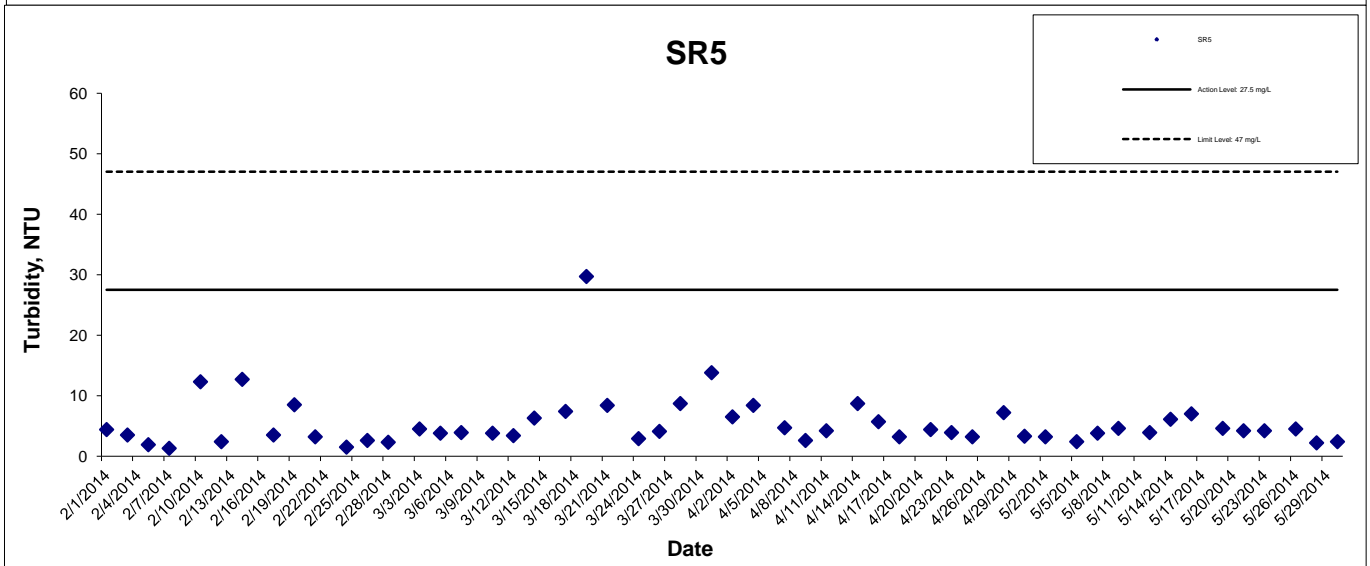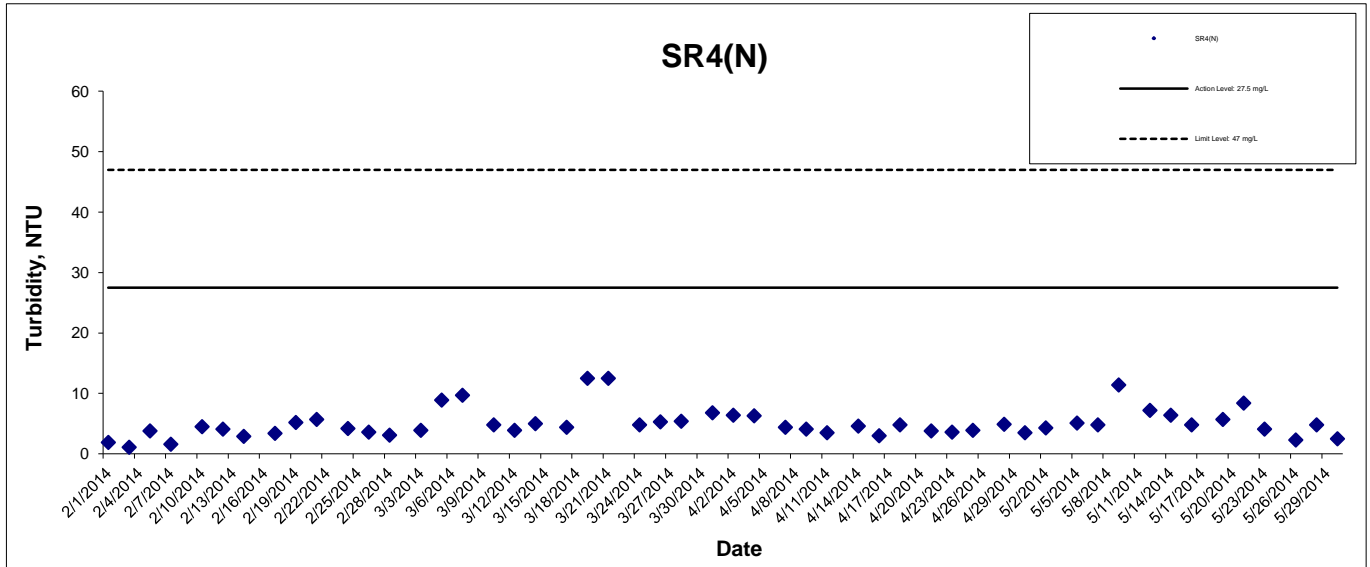

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.




Turbidity at Mid-Ebb Tide

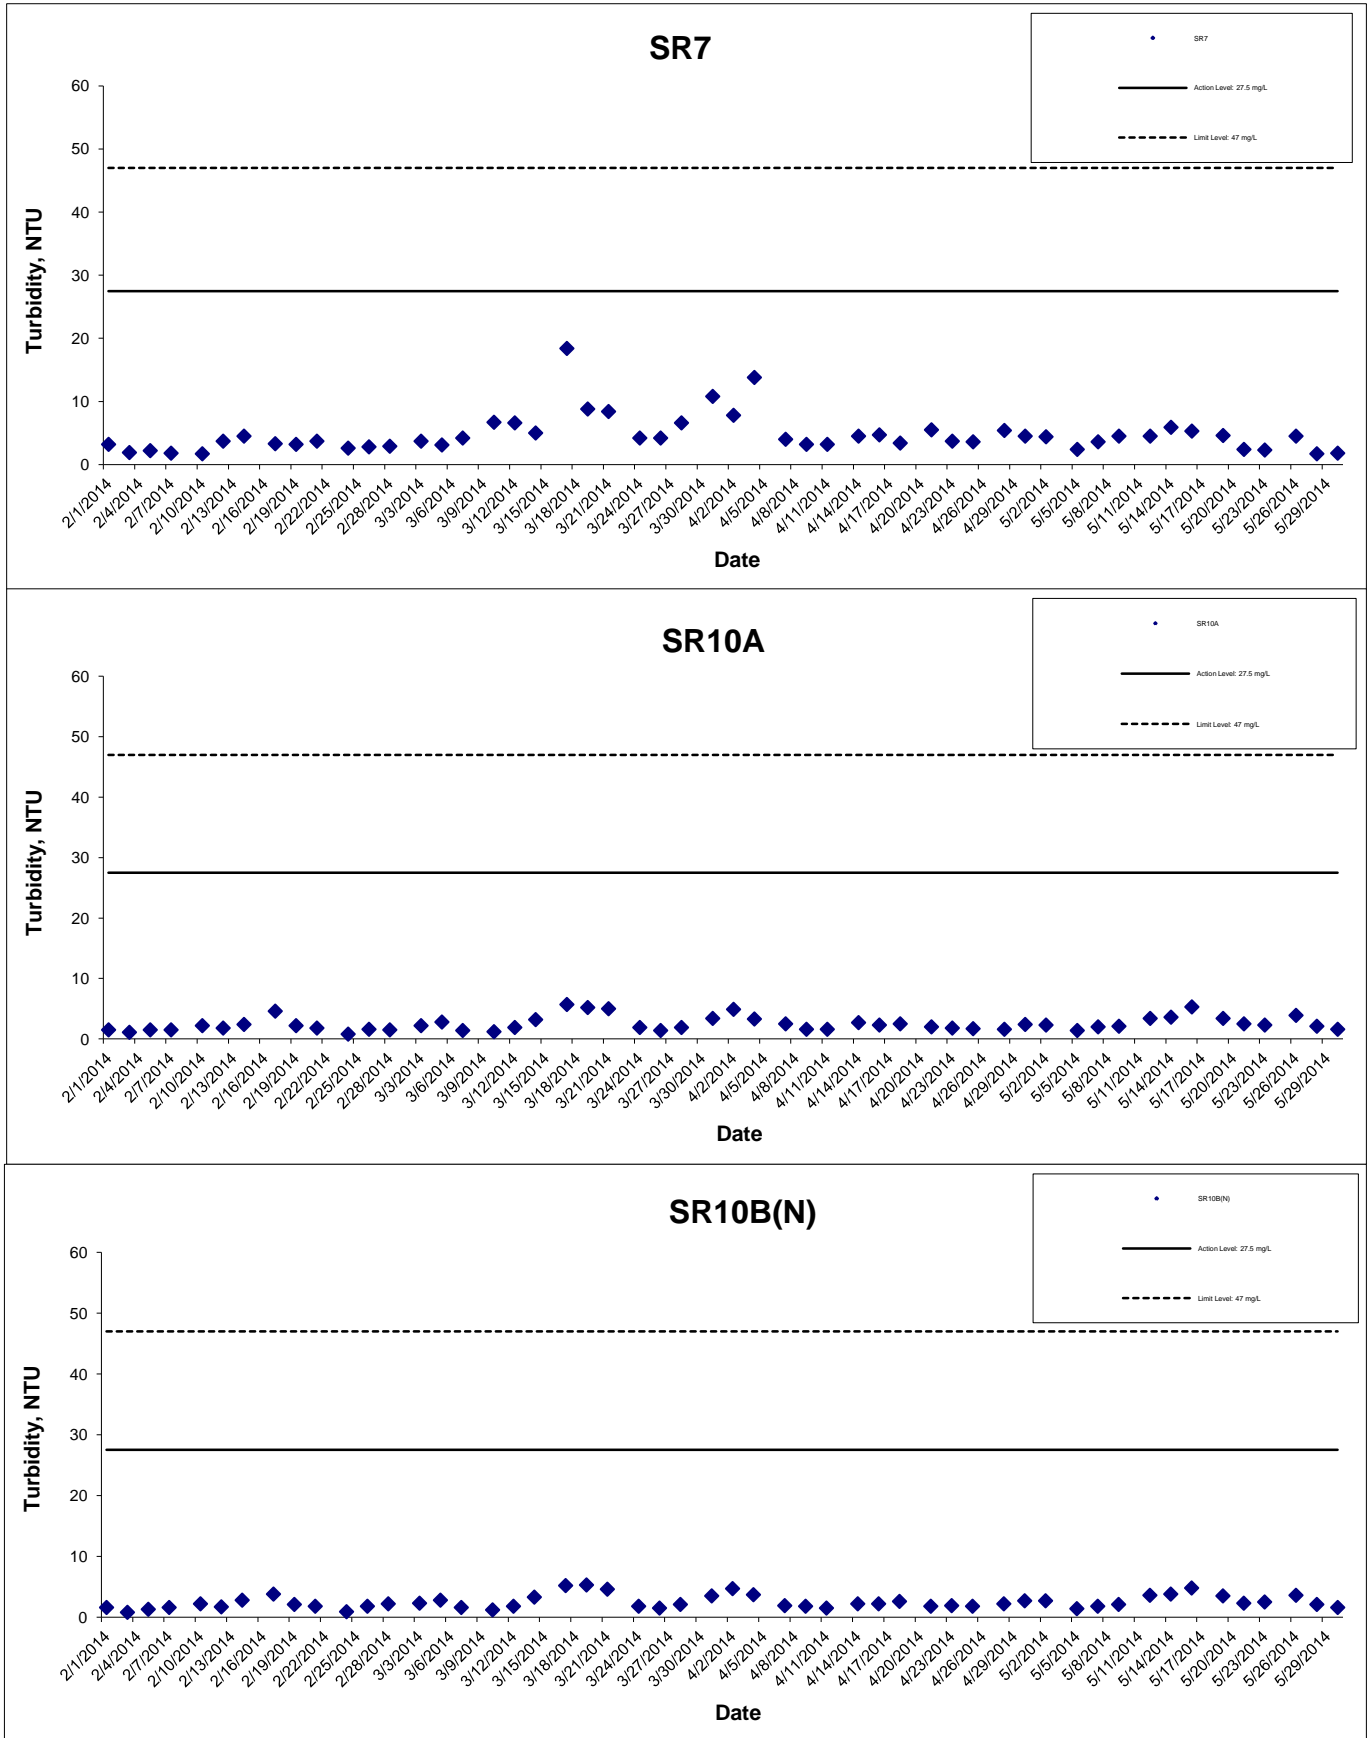

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.






Turbidity at Mid-Flood Tide

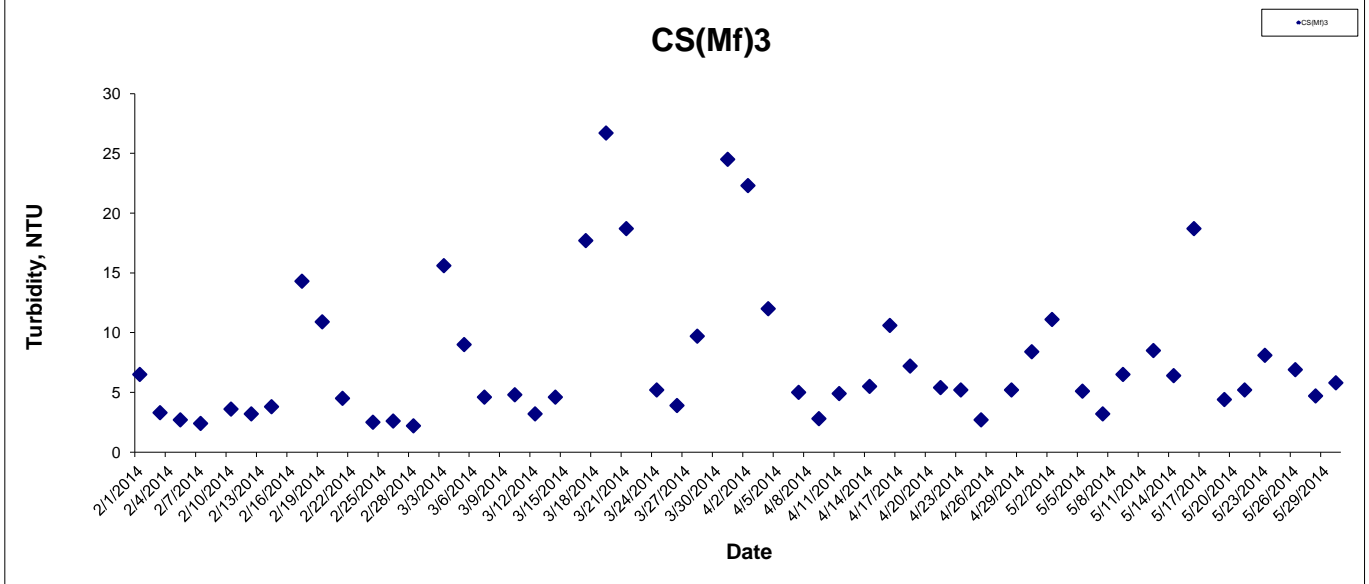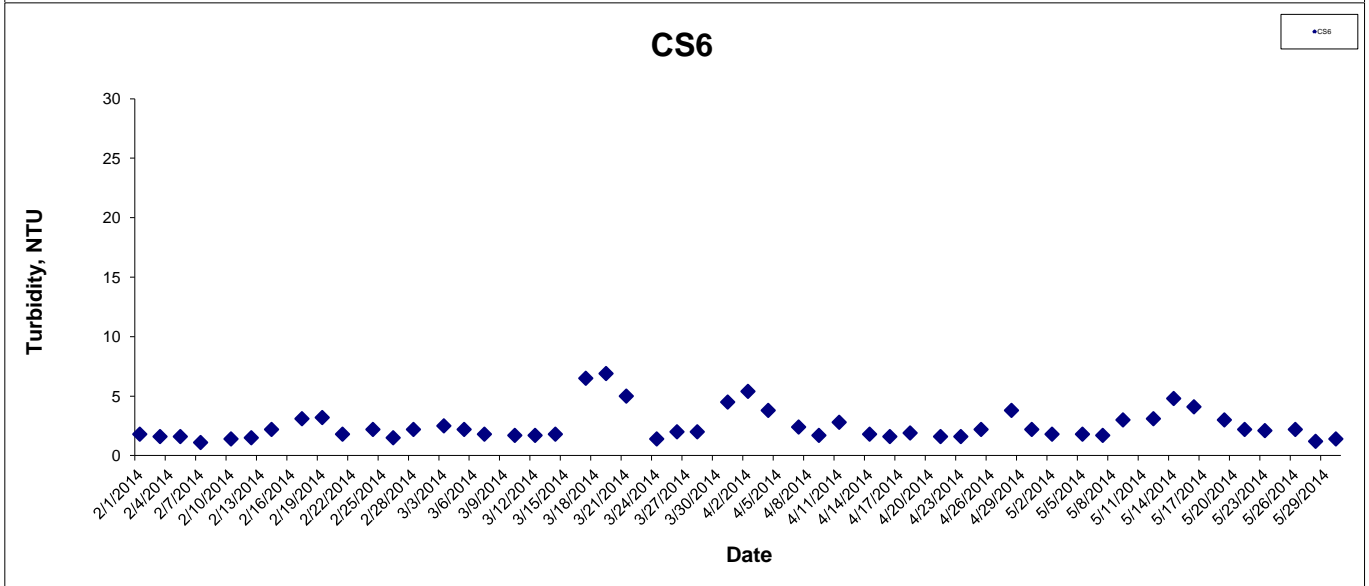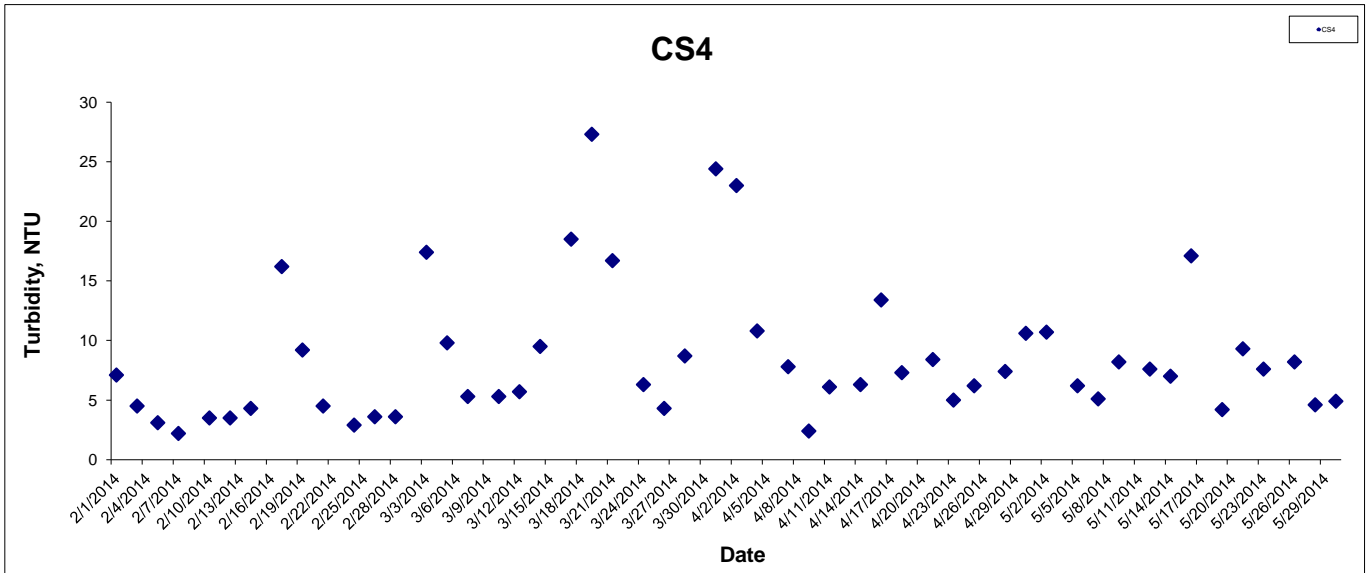

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.




Turbidity at Mid-Flood Tide

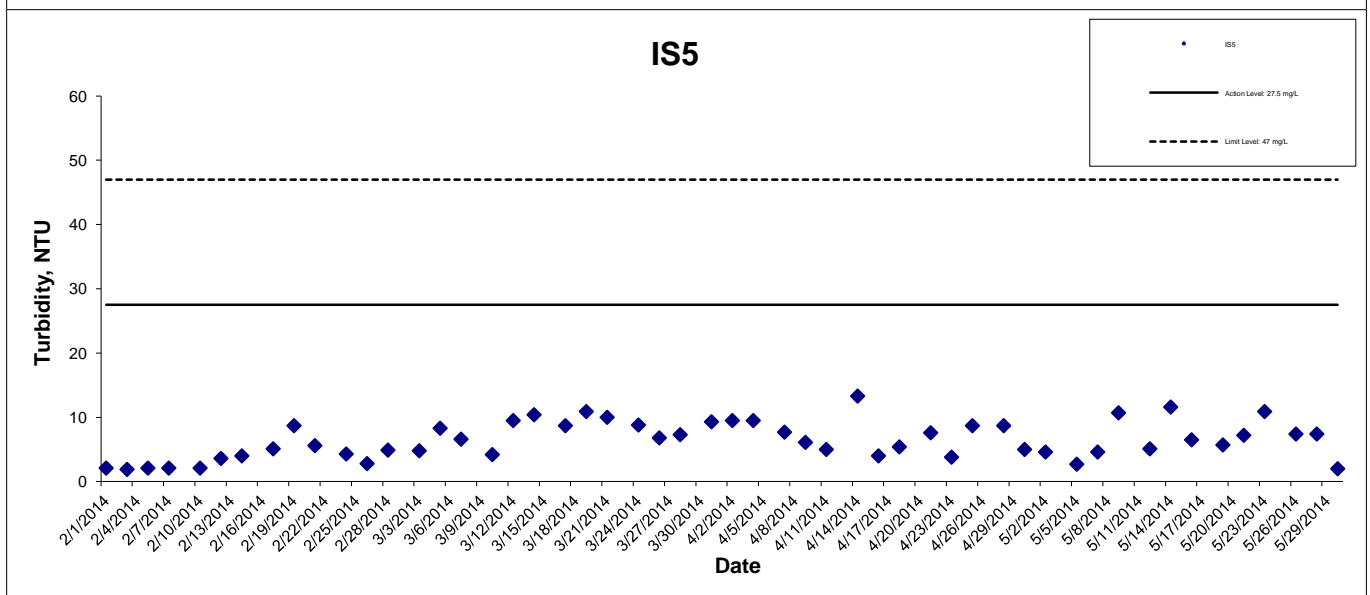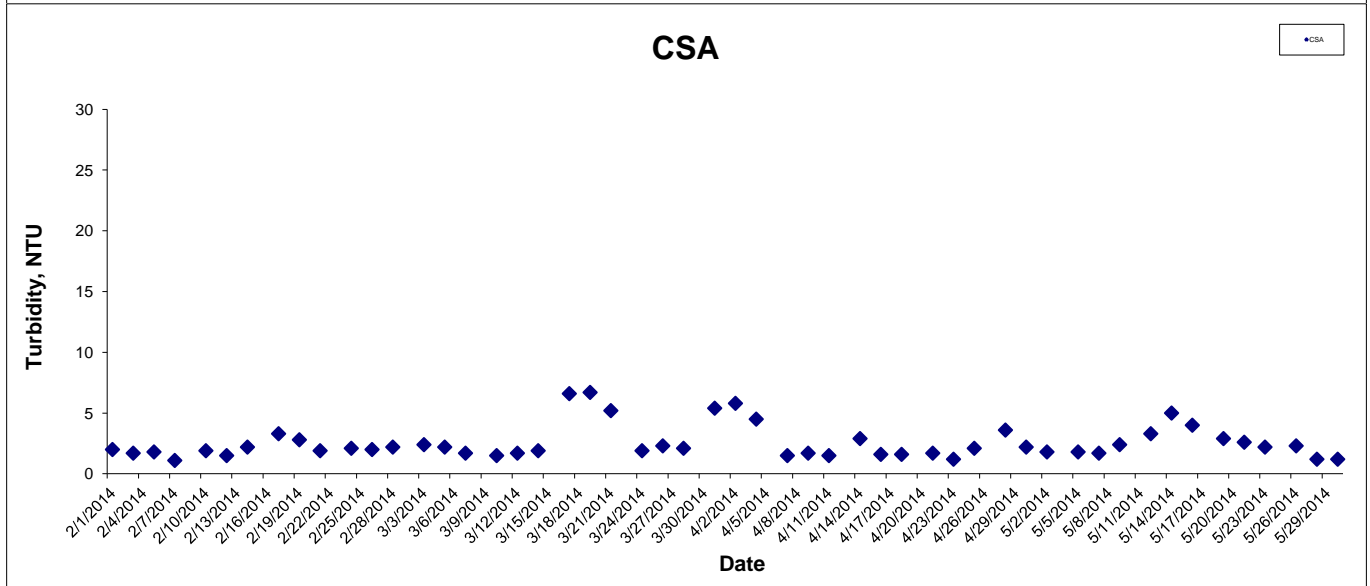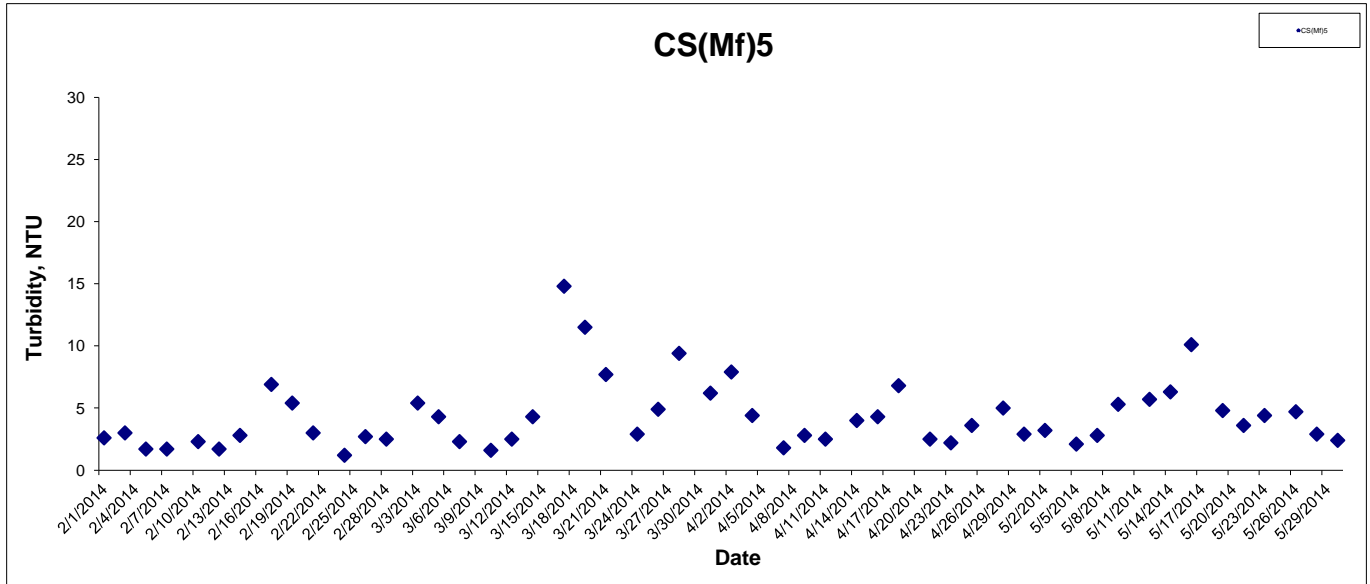

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.






Turbidity at Mid-Flood Tide

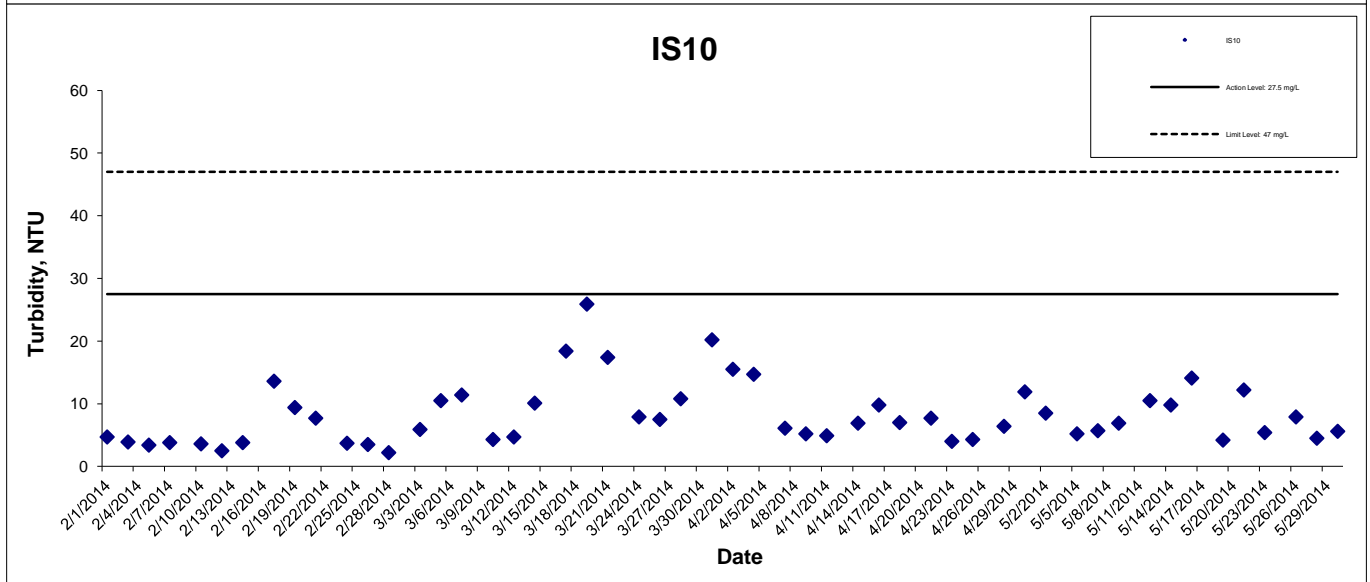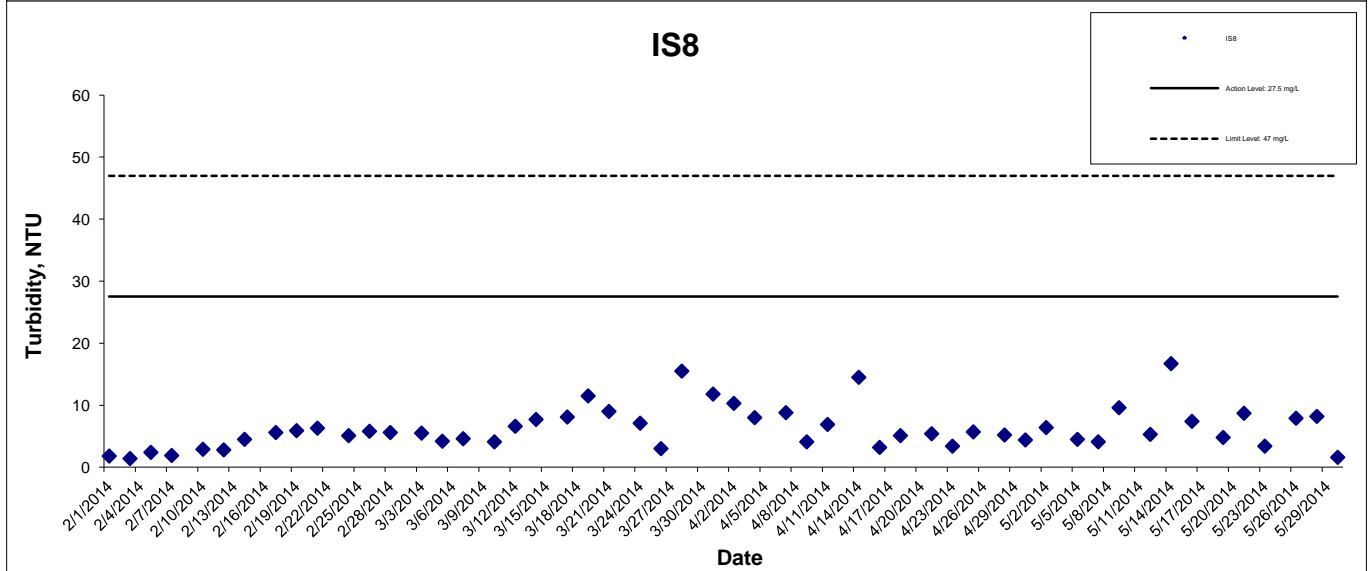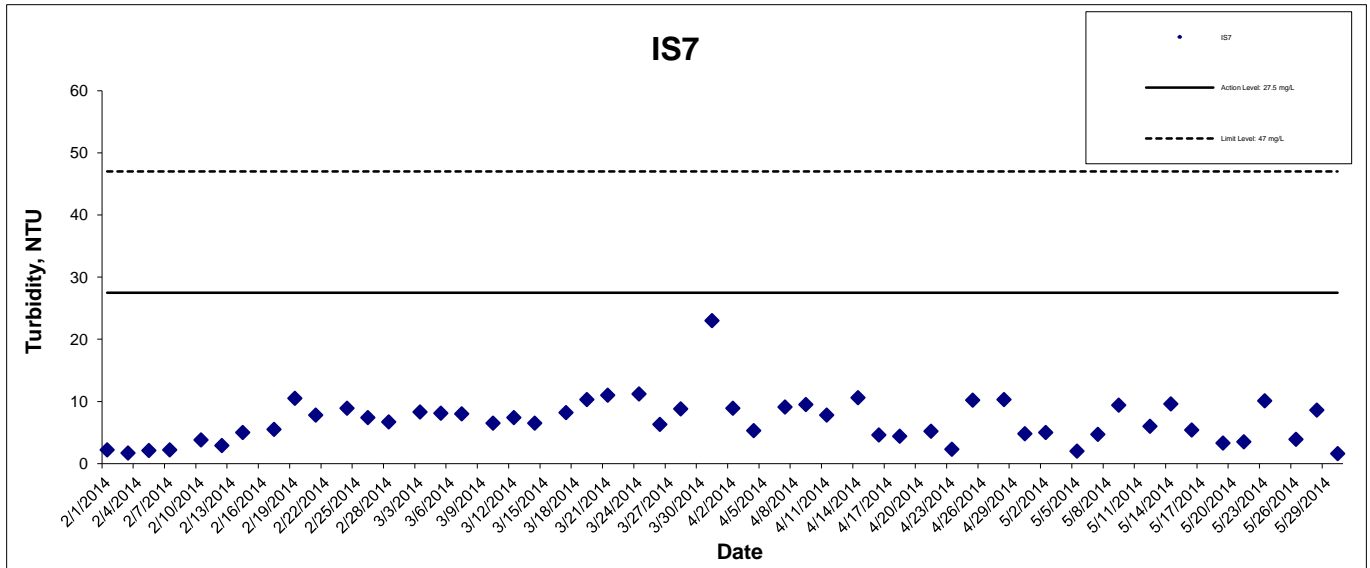




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Flood Tide

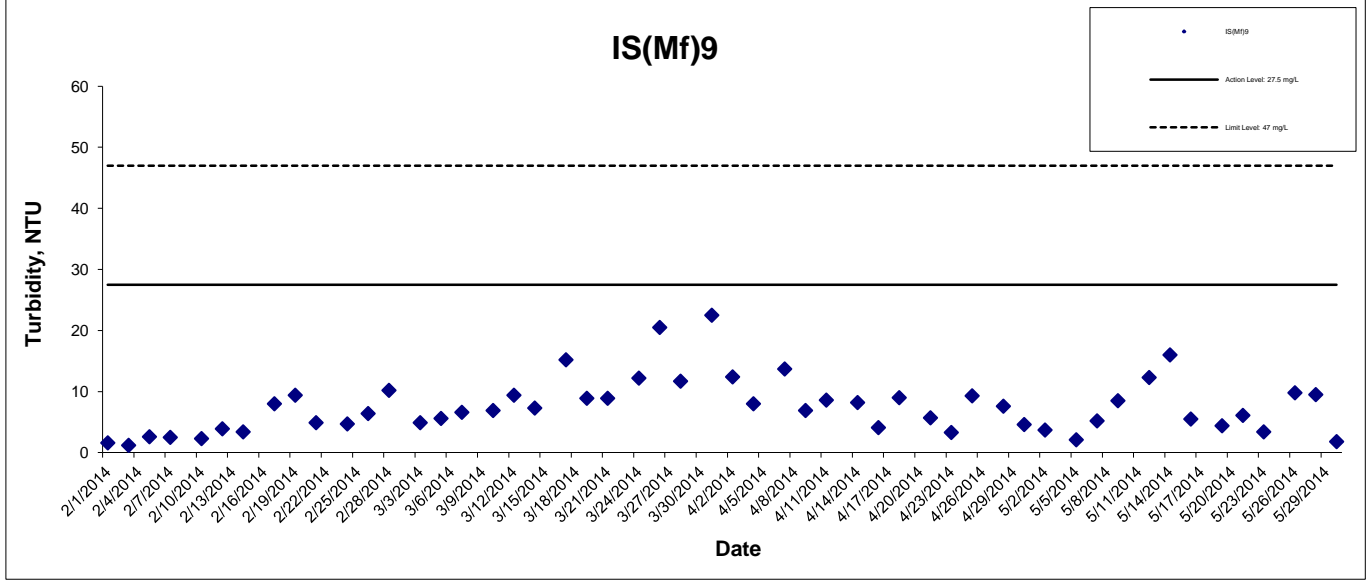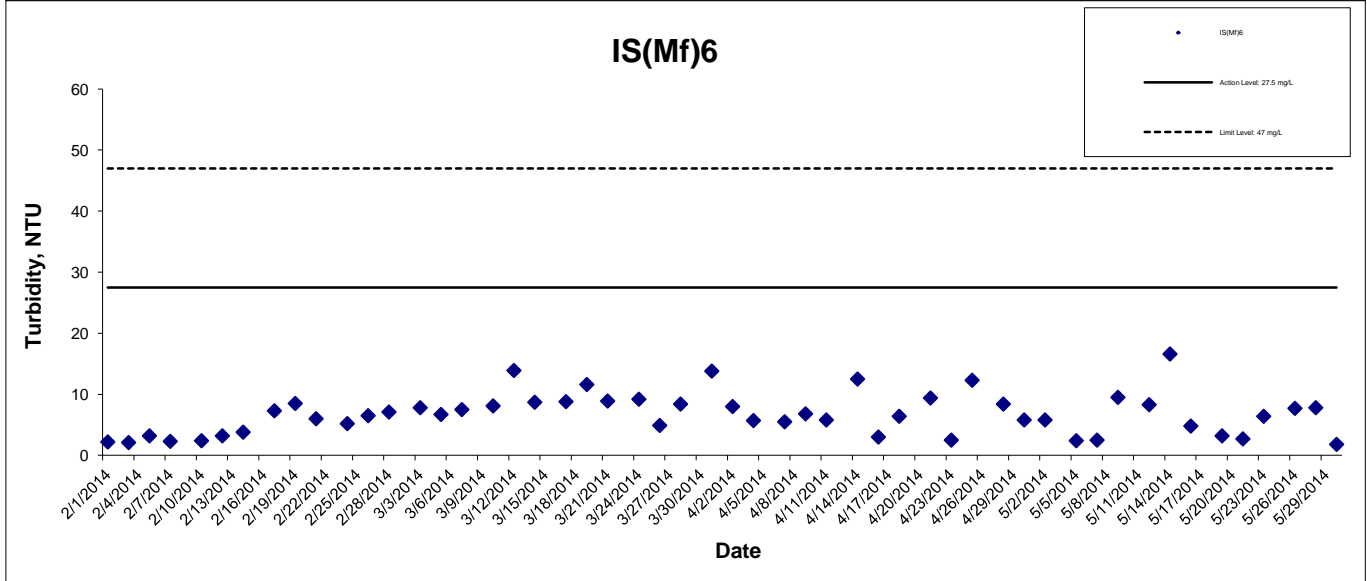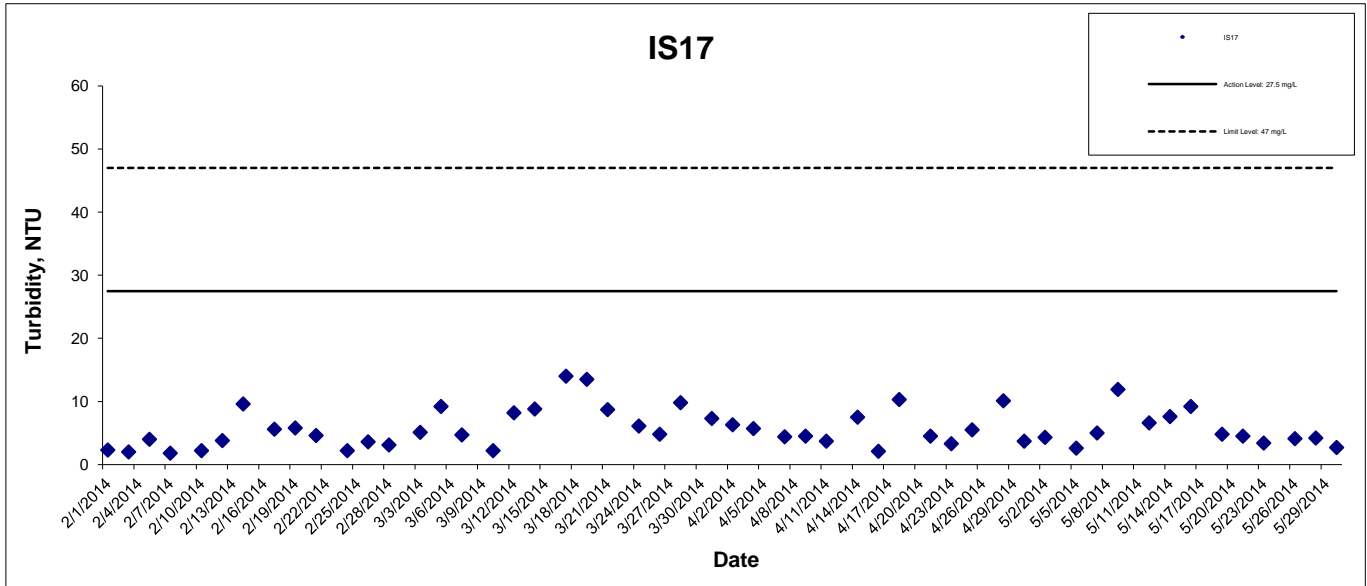




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Flood Tide

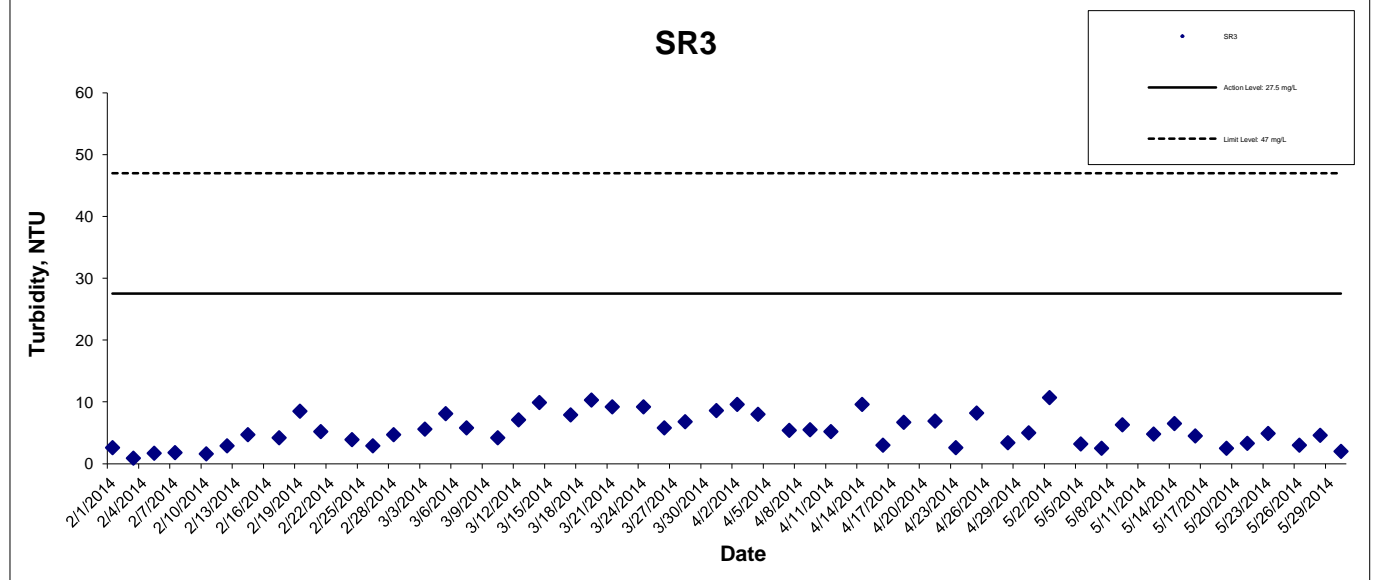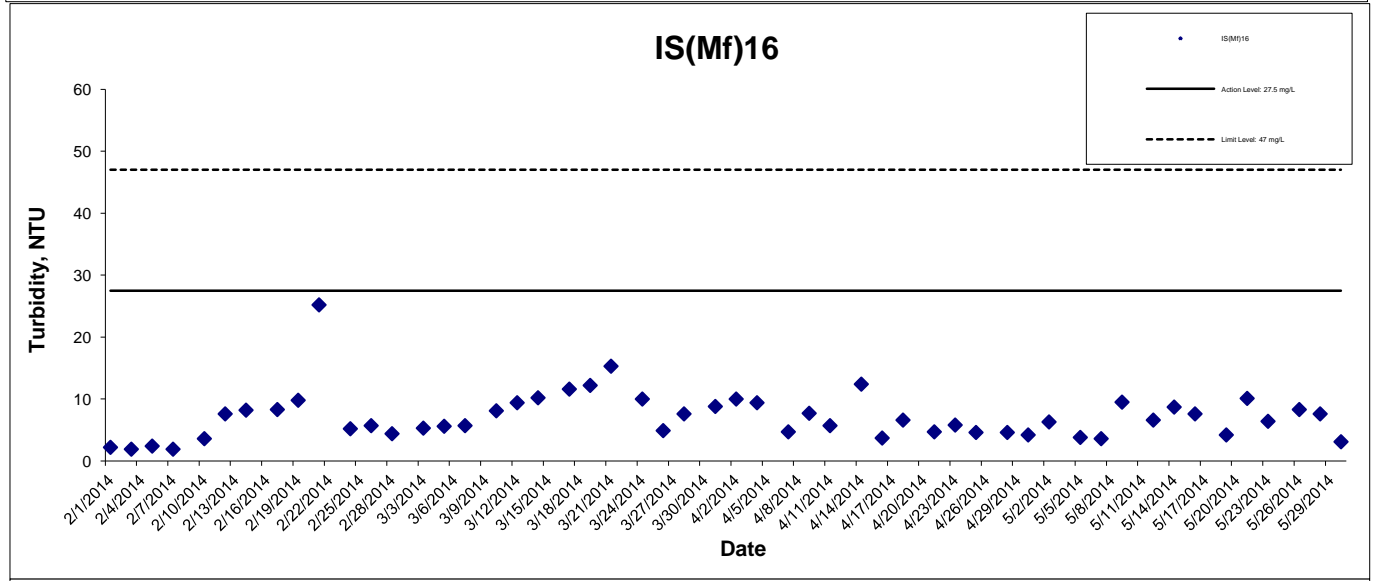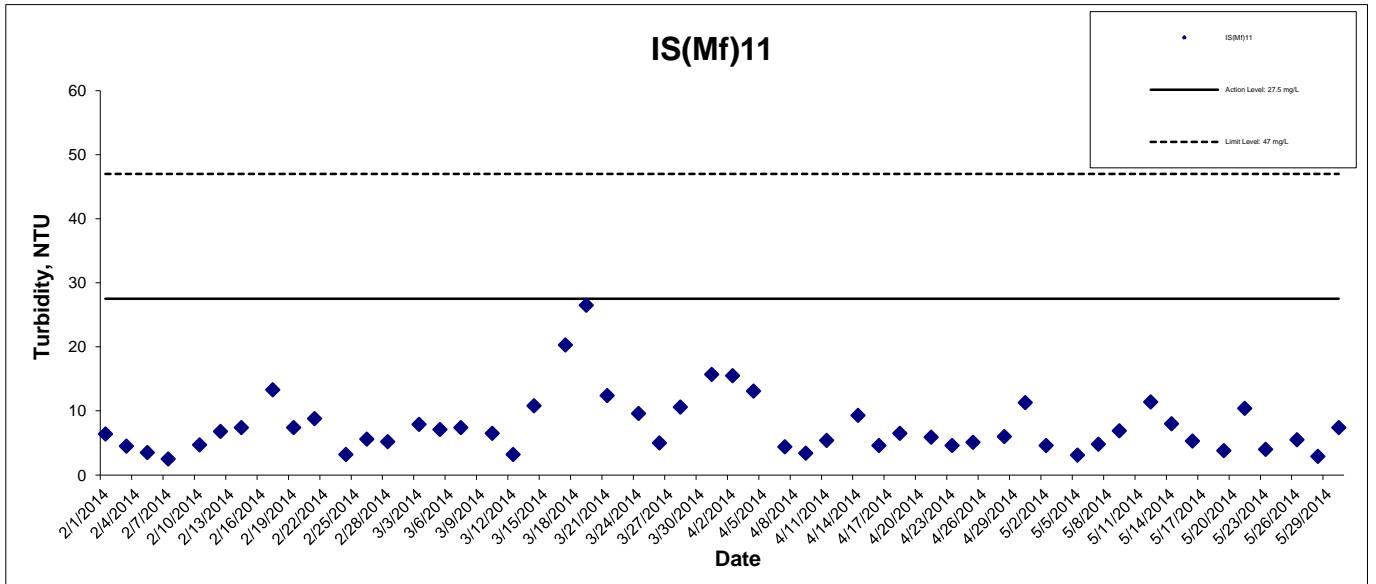

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Turbidity at Mid-Flood Tide

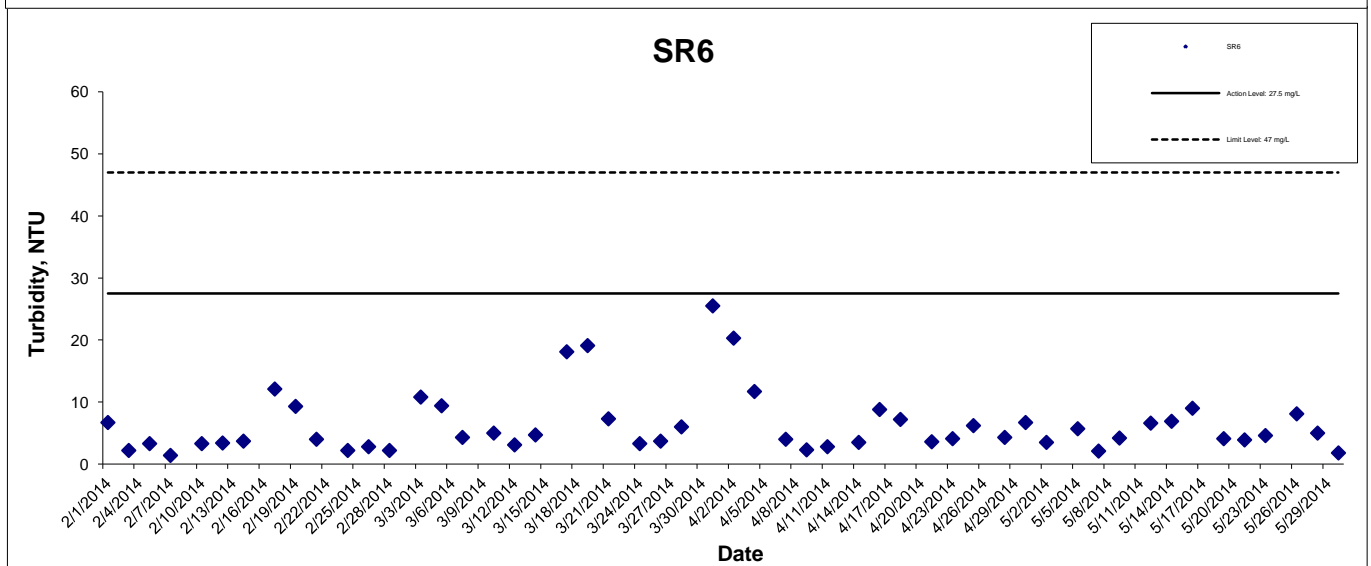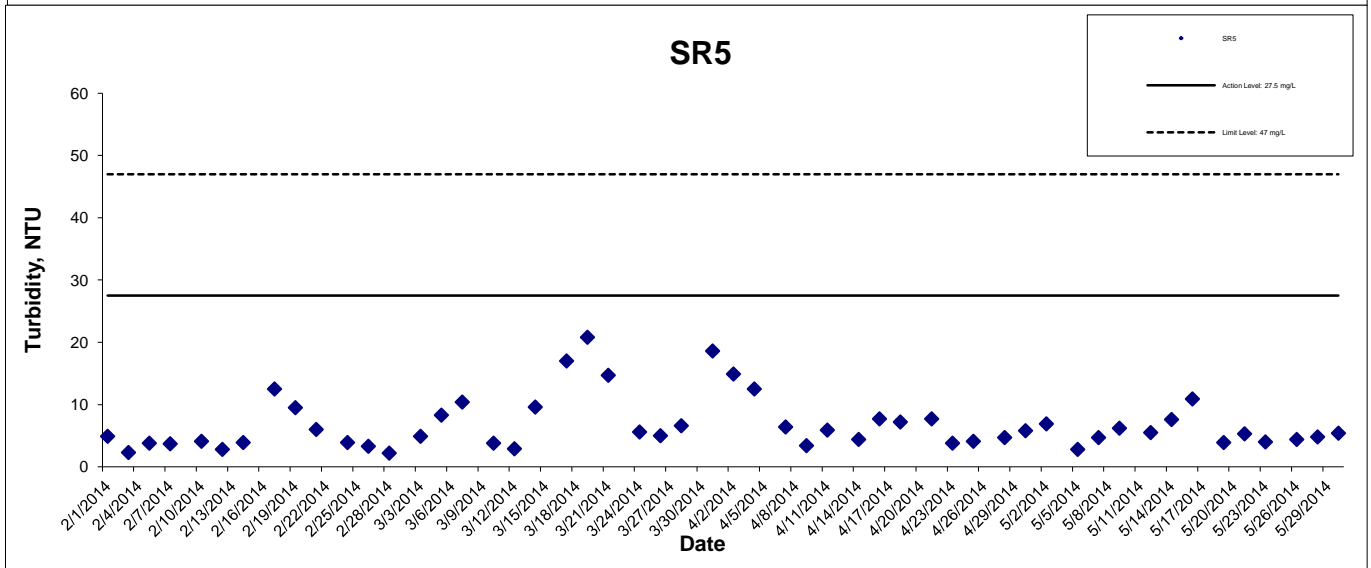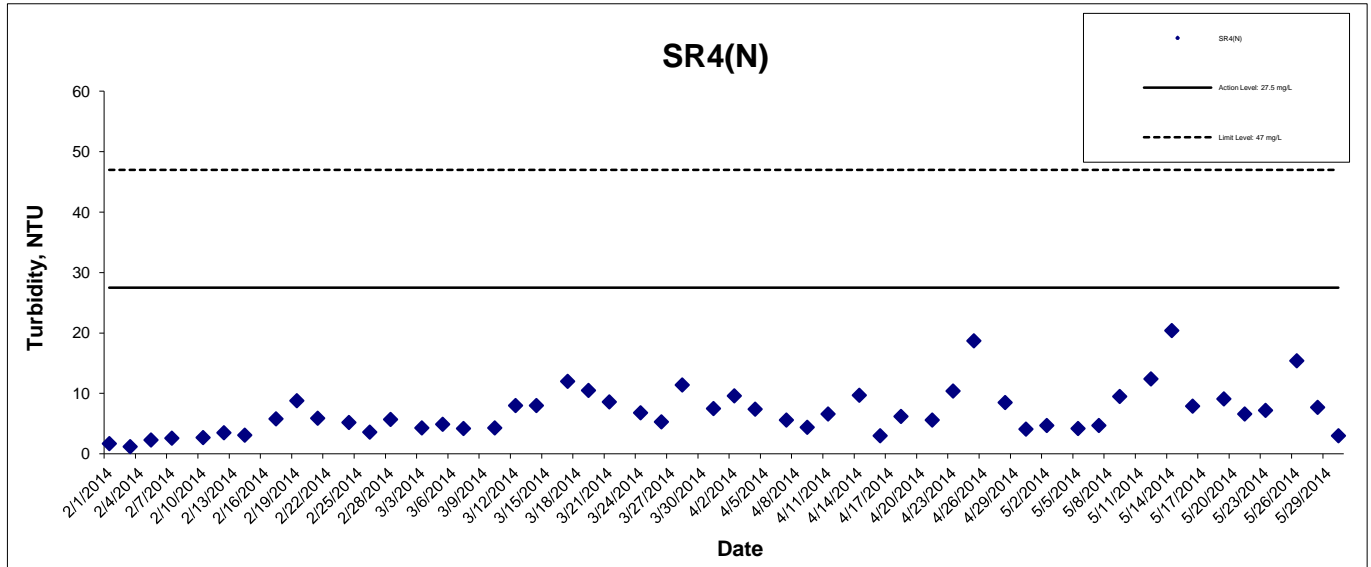




This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

HONG KONG - ZHUHAI - MACAO BRIDGE
HONG KONG BOUNDARY CROSSING FACILITIES
- RECLAMATION WORKS

Graphical Presentation of Impact Water Quality
Monitoring Results



Turbidity at Mid-Flood Tide

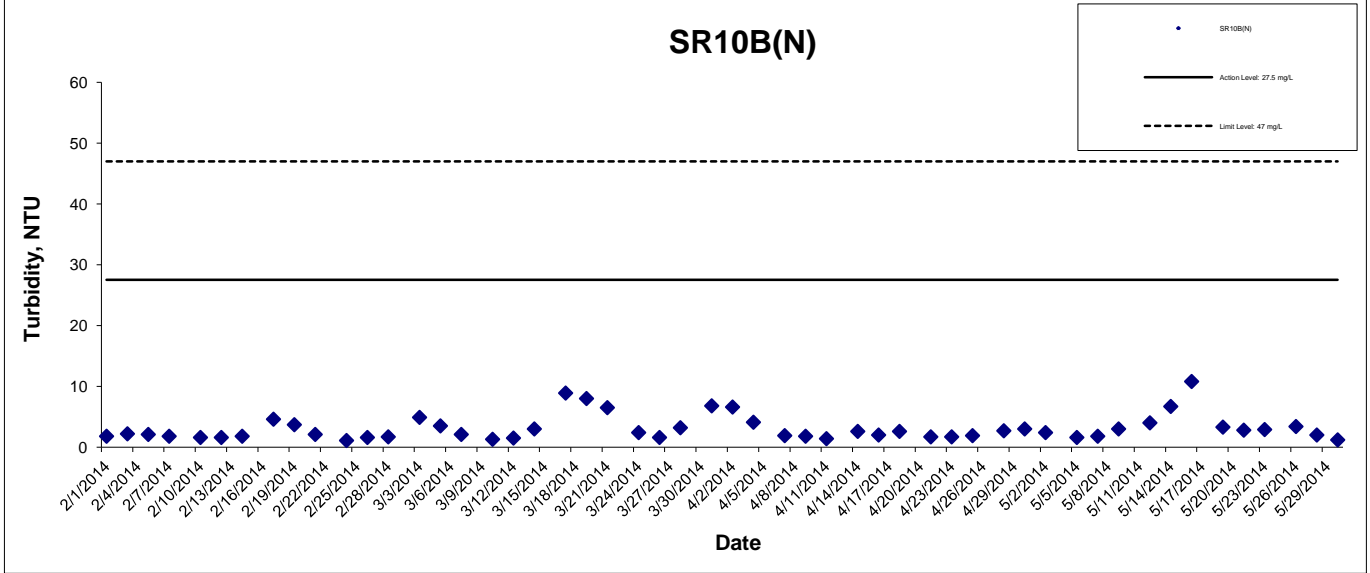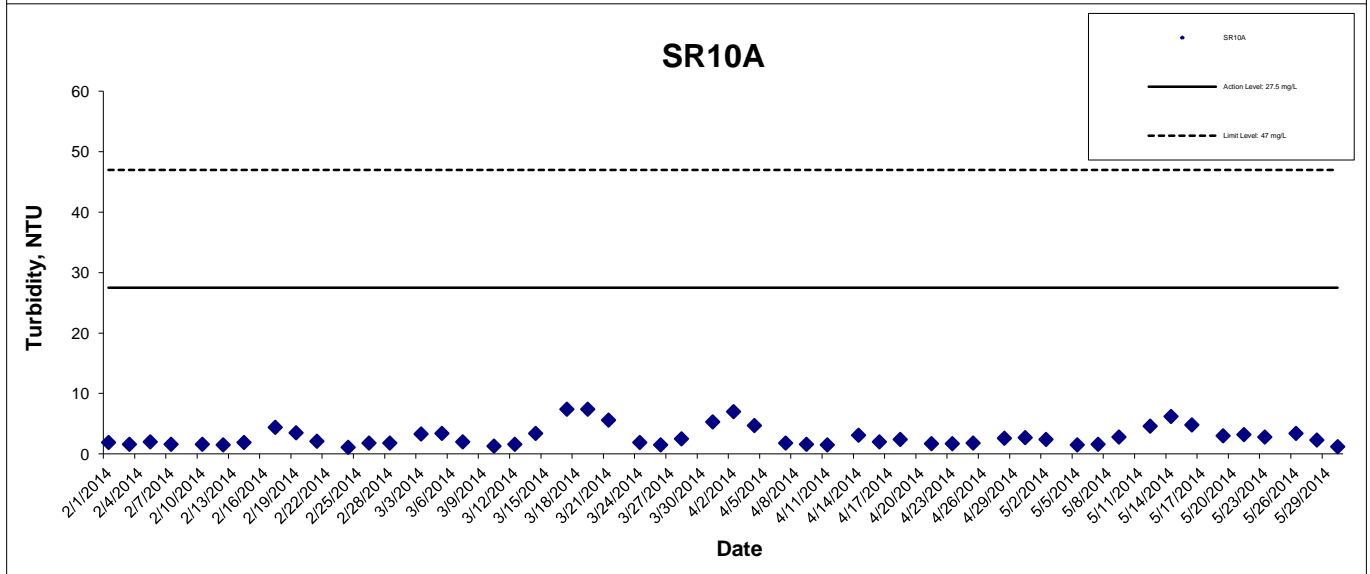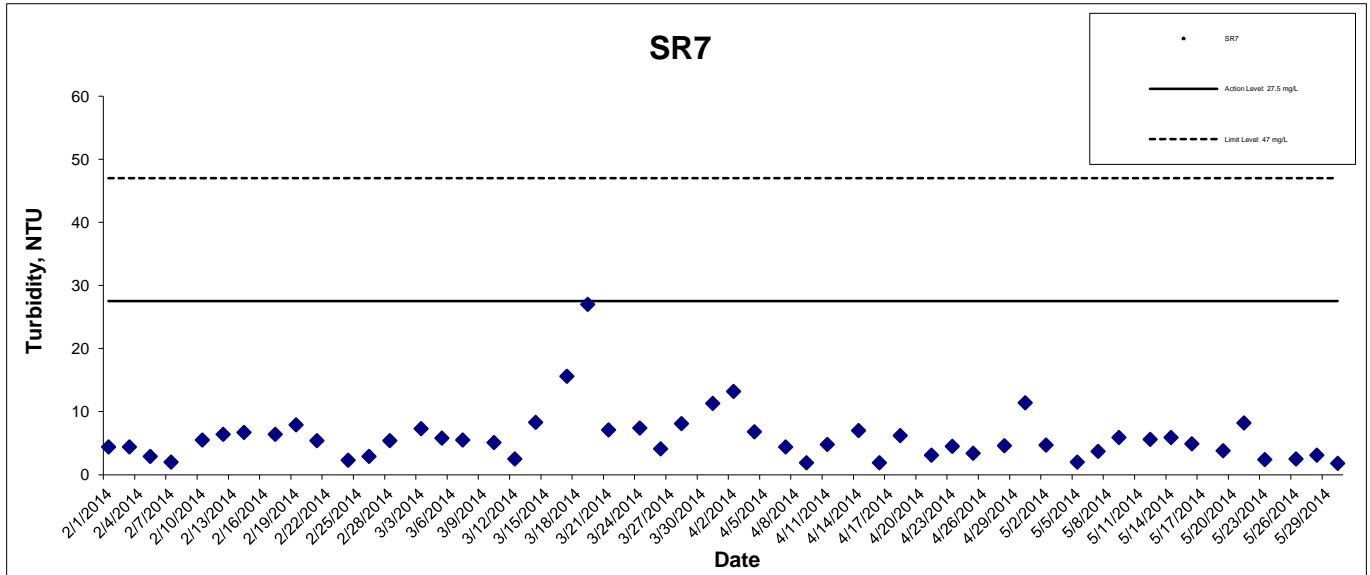

This Drawing has been prepared for the use of AECOM's client. It Dec not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent.

Appendix K Impact Dolphin Monitoring Survey Sighting Summary

Table 1 Impact Dolphin Monitoring Survey Sighting Table

Project	Contract	Date	Sighting No.	Time	Group Size	Area	Beaufort	PSD	Effort	Type	Northing	Easting	Season	Boat Association
HKBCF	HY/2010/02	31/05/14	951	9:28	12	NWL	1	N/A	Opp	Impact	814559	804547	Spring	No
HKBCF	HY/2010/02	31/05/14	953	11:10	3	NWL	1	124	On	Impact	821819	804685	Spring	No
HKBCF	HY/2010/02	31/05/14	954	13:26	3	NWL	2	N/A	Opp	Impact	816110	805426	Spring	No

KEY:

Sighting

Opp Opportunistic
 On On effort

PSD

Perpendicular Sighting Distance

Group Size

Represents best estimate for group encountered

NEL

North East Lantau

NWL

North West Lantau

April 2014 Photo Identification Information

Table 2. Sightings of Individually Identified Chinese White Dolphin (*Sousa chinensis*) between March 2012 – April 2014

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
HZMB 119		2014-04-19	940	NWL
HZMB 118		2014-01-06	890	NWL
HZMB 117		2014-01-06	888	NWL
HZMB 116		2013-12-26	879	NWL
HZMB 115		2013-12-26	879	NWL
HZMB 114		2013-10-24	827	NWL
HZMB 113		2013-10-24	827	NWL
HZMB 112		2013-10-15	815	NWL
HZMB111		2013-10-15	815	NWL
HZMB 110		2013-10-15	812	NWL
HZMB 108		2013-08-30	780	NEL
HZMB 107		2013-08-21	770	NWL
HZMB 106		2013-08-21	769	NWL
HZMB 105		2013-07-08	711	NWL
HZMB 104		2013-07-08	711	NWL
HZMB 103		2013-07-08	711	NWL
HZMB 102		2013-07-08	706	NWL
HZMB 101		2013-07-08	706	NWL
HZMB 100		2013-07-08	706	NWL
HZMB 099		2013-06-13	681	NWL
		2013-06-13	680	NWL
HZMB 098	NL104	2014-01-06	888	NWL
		2013-11-02	849	NWL
		2013-11-02	845	NWL
		2013-10-24	831	NWL
		2013-07-08	711	NWL
		2013-05-24	659	NWL
HZMB 097		2013-05-09	647	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
HZMB 096		2013-04-01	621	NWL
HZMB 095		2013-08-30	780	NEL
		2013-06-25	697	NWL
		2013-06-13	682	NWL
		2013-04-01	621	NWL
HZMB 094		2014-02-17	910	NWL
		2013-06-26	703	NWL
		2013-06-25	698	NWL
		2013-03-18	601	NWL
HZMB 093		2013-05-24	657	NWL
		2013-02-21	587	NWL
HZMB 092		2013-02-21	589	NWL
		2013-02-15	581	NWL
HZMB 091		2013-02-15	579	NWL
HZMB 090		2013-06-25	697	NWL
		2013-06-13	682	NWL
		2013-02-15	579	NWL
HZMB 089		2013-02-15	579	NWL
HZMB 088		2013-02-15	579	NWL
HZMB 087		2013-02-15	579	NWL
HZMB 086	NL242	2013-05-09	642	NWL
		2013-02-15	579	NWL
		2011-10-10	Baseline	NWL
HZMB 085		2013-06-26	703	NWL
		2013-02-15	579	NWL
HZMB 084		2013-02-14	575	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
HZMB 083	NL136	2013-12-19	863	NWL
		2013-03-28	607	NWL
		2013-02-15	579	NWL
		2013-01-28	568	NWL
		2012-01-28	564	NWL
HZMB 082		2013-02-21	587	NWL
		2013-02-15	579	NWL
		2013-01-28	563	NWL
HZMB 081		2013-01-28	559	NWL
		2013-01-28	557	NWL
HZMB 080		2013-01-28	556	NWL
HZMB 079		2013-01-28	556	NWL
HZMB 078		2013-02-15	579	NWL
		2013-01-08	552	NWL
HZMB 077		2013-12-26	878	NWL
		2013-07-08	706	NWL
		2012-12-11	541	NWL
HZMB 076		2013-07-08	706	NWL
		2012-12-11	541	NWL
HZMB 075		2012-12-06	525	NEL
HZMB 074		2013-05-09	647	NWL
		2013-04-01	623	NWL
		2013-04-01	621	NWL
		2013-02-21	594	NEL
		2012-12-10	529	NEL
		2012-12-06	525	NEL
HZMB 073		2013-05-09	647	NWL
		2013-04-01	623	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		2013-04-01	621	NWL
		2013-02-21	594	NEL
		2012-12-10	529	NEL
		2012-12-06	525	NEL
HZMB 072		2012-10-24	476	NWL
HZMB 071		2012-10-24	475	NWL
		2012-10-12	466	NWL
HZMB 070		2012-10-24	476	NWL
HZMB 069		2013-08-21	774	NWL
		2013-07-08	711	NWL
		2012-10-24	476	NWL
HZMB 068		2013-11-01	839	NWL
		2012-10-24	476	NWL
HZMB 067		2012-10-24	475	NWL
HZMB 066	NL93	2013-01-28	559	NWL
		2012-12-11	537	NWL
		2012-10-24	475	NWL
		2012-10-12	466	NWL
HZMB 064		2013-05-09	647	NWL
		2013-01-28	561	NWL
		2012-10-24	475	NWL
		2012-10-12	466	NWL
HZMB 063		2013-05-09	647	NWL
		2012-10-12	466	NWL
HZMB 062		2012-12-06	525	NEL
		2012-10-11	457	NWL
HZMB 060		2012-09-18	447	NWL
HZMB 059		2013-02-21	591	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		2012-09-18	445	NWL
HZMB 057		2012-09-18	440	NWL
HZMB 056		2012-09-18	442	NWL
		2012-09-05	433	NEL
HZMB 055		2012-09-04	425	NWL
HZMB 054	CH34	2014-01-06	888	NWL
		2013-11-07	854	NWL
		2013-11-02	845	NWL
		2013-10-24	831	NWL
		2013-08-30	780	NEL
		2013-07-08	711	NWL
		2013-09-18	448	NWL
		2012-09-05	432	NEL
		2011-11-07	Baseline	NWL
		2011-11-05	Baseline	NWL
		2011-11-02	Baseline	NWL
		2011-11-01	Baseline	NEL
		2011-11-01	Baseline	NEL
		2011-10-28	Baseline	NWL
2011-10-06	Baseline	NWL		
HZMB 053		2012-09-04	425	NWL
HZMB 052		2012-09-04	423	NWL
HZMB 051	NL213	2013-05-09	644	NWL
		2013-04-01	622	NWL
		2013-02-15	582	NWL
		2013-02-15	581	NWL
		2013-01-28	559	NWL
		2013-01-28	556	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		2012-09-04	422	NWL
HZMB 050		2014-01-10	900	NWL
		2014-01-06	888	NWL
		2013-02-15	579	NWL
		2012-09-04	421	NWL
HZMB 049		2012-09-03	419	NWL
HZMB 048		2012-09-03	419	NWL
HZMB 047		2012-09-03	412	NWL
HZMB 046		2012-09-03	412	NWL
HZMB 045		2014-02-17	910	NWL
		2013-06-13	682	NWL
		2013-02-15	579	NWL
		2012-11-01	495	NWL
HZMB 044	NL98	2014-02-17	910	NWL
		2013-12-19	864	NWL
		2013-11-02	845	NWL
		2013-11-01	842	NWL
		2013-10-15	819	NWL
		2013-05-09	648	NWL
		2013-05-09	647	NWL
		2013-04-01	623	NWL
		2013-04-01	621	NWL
		2013-02-15	579	NWL
2012-11-01	495	NWL		
HZMB 043		2012-09-03	407	NWL
HZMB 042	NL260	2013-12-19	863	NWL
		2012-11-01	495	NWL
		2011-11-07	Baseline	NWL
HZMB 041	NL24	2014-02-17	910	NWL
		2013-11-02	845	NWL
		2013-05-09	648	NWL
		2013-05-09	647	NWL
		2013-04-01	623	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		2013-04-01	621	NWL
		2013-02-15	579	NWL
		2012-11-01	495	NWL
		2011-11-06	Baseline	NEL
		2011-11-05	Baseline	NWL
		2011-11-05	Baseline	NWL
		2011-10-10	Baseline	NWL
HZMB 040		2014-02-17	910	NWL
		2014-01-06	893	NWL
		2013-10-15	821	NWL
		2013-07-08	714	NWL
		2013-07-08	711	NWL
		2013-02-21	589	NWL
		2012-11-01	493	NWL
HZMB 038		2012-11-01	490	NWL
HZMB 037		2012-11-01	490	NWL
HZMB 036		2012-09-03	407	NWL
		2012-11-01	490	NWL
HZMB 035		2013-02-15	579	NWL
		2012-11-01	490	NWL
HZMB 034		2012-11-01	493	NWL
HZMB 028		2013-04-01	625	NWL
		2012-08-06	373	NWL
HZMB 027		2013-12-19	863	NWL
		2013-02-15	579	NWL
		2013-01-28	568	NWL
		2013-01-28	564	NWL
		2012-06-14	299	NWL
HZMB 026		2013-06-25	697	NWL
		2013-05-09	642	NWL
		2013-01-28	561	NWL
		2012-06-13	295	NEL
HZMB 025		2013-02-22	596	NEL
		2013-02-21	591	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		2012-12-06	525	NEL
		2012-10-11	457	NWL
		2012-06-13	295	NEL
HZMB 024		2013-03-18	601	NWL
		2012-06-13	295	NEL
HZMB 023		2014-01-06	888	NWL
		2013-07-08	715	NWL
		2013-07-08	711	NWL
		2013-04-01	619	NWL
		2013-02-21	589	NWL
		2013-02-15	579	NWL
		2012-07-10	330	NWL
HZMB 022		2014-01-06	888	NWL
		2013-10-24	827	NWL
		2013-07-08	715	NWL
		2013-07-08	711	NWL
		2013-04-01	619	NWL
		2013-02-21	589	NWL
		2013-02-15	579	NWL
		2012-07-10	330	NWL
HZMB 021	NL37	2012-07-10	330	NWL
		2011-09-16	Baseline	NWL
HZMB 020		2012-07-10	330	NWL
HZMB 019		2012-07-10	330	NWL
HZMB 018		2014-02-17	910	NWL
		2013-05-09	647	NWL
		2013-02-21	594	NEL
		2012-12-10	529	NEL
		2012-07-10	330	NWL
HZMB 017		2012-07-10	330	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
HZMB 016		2013-07-08	706	NWL
		2012-12-11	539	NWL
		2012-09-18	446	NWL
		2012-09-04	421	NWL
		2012-07-10	330	NWL
HZMB 015		2012-07-10	330	NEL
HZMB 014	NL176	2013-12-26	880	NWL
		2012-08-06	373	NWL
		2012-06-13	295	NEL
		2011-11-06	Baseline	NEL
		2011-11-01	Baseline	NEL
		2011-11-01	Baseline	NEL
HZMB 013		2012-05-28	281	NWL
HZMB 012		2012-05-28	281	NWL
HZMB 011	EL01	2013-02-22	597	NEL
		2013-02-21	592	NEL
		2013-02-14	572	NEL
		2012-11-06	517	NEL
		2012-09-19	452	NWL
		2012-03-31	261	NEL
		2011-11-02	Baseline	NWL
		2011-11-01	Baseline	NEL
HZMB 009		2012-05-28	281	NWL
HZMB 008		2012-05-28	281	NWL
HZMB 007	NL246	2012-12-10	529	NEL
HZMB 006		2013-02-21	594	NEL
		2012-12-11	539	NWL
		2012-11-01	495	NWL

Contract No. HY/2010/02
 Hong Kong-Zhuhai-Macao Bridge
 Hong Kong Boundary Crossing Facilities – Reclamation Works
 Monthly EM&A Report for May 2014

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		2012-03-29	250	NWL
HZMB 005		2013-11-09	860	NWL
		2013-11-07	858	NWL
		2013-10-15	813	NWL
		2012-12-10	532	NWL
		2012-08-06	374	NWL
		2012-05-28	287	NWL
HZMB 004		2012-09-04	421	NWL
		2012-03-31	262	NWL
HZMB 003	NL179	2014-10-15	812	NWL
		2013-06-25	697	NWL
		2012-12-10	529	NEL
		2012-03-31	261	NWL
		2011-11-06	Baseline	NEL
		2011-09-16	Baseline	NWL
HZMB 002	WL111	2013-12-26	878	NWL
		2013-12-19	863	NWL
		2013-11-01	839	NWL
		2013-10-15	819	NWL
		2013-09-24	798	NWL
		2013-02-14	573	NWL
		2012-12-11	536	NWL
		2012-12-11	535	NWL
		2012-10-12	466	NWL
		2012-10-24	475	NWL
		2012-05-28	281	NWL
		2012-03-29	250	NWL
HZMB 001	WL46	2013-08-21	771	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
		2013-06-13	681	NWL
		2013-04-01	617	NWL
		2013-02-14	573	NWL
		2012-03-29	250	NWL

Identification Number	Baseline Identification Number	Date (YYYY-MM-DD)	Sighting Number	Area Sighted
	CH98	2011-11-02	Baseline	NWL
	NL11	2011-11-02	Baseline	NWL
		2011-11-07	Baseline	NWL
	NL12	2011-11-02	Baseline	NWL
	NL33	2011-09-23	Baseline	NWL
		2011-11-01	Baseline	NEL
		2011-11-05	Baseline	NWL
		2011-11-07	Baseline	NWL
	NL37	2011-09-16	Baseline	NWL
	NL46	2011-10-28	Baseline	NWL

HZMB 119 2014-04-19_10-55-28



Appendix L – Event Action Plan

Event / Action Plan for Air Quality

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level				
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
Limit Level				
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Event / Action Plan for Construction Noise

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify IEC and Contractor; 2. Identify source, investigate the causes of exceedance and propose remedial measures; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC; 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Inform IEC, ER, EPD and Contractor; 2. Identify source; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Event / Action Plan for Water Quality

Event	Action			
	ET Leader	IEC	ER	Contractor
Action level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat <i>in situ</i> measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, contractor and ER; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Repeat measurement on next day of exceedance to confirm findings. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working methods; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; 4. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of non-compliance in writing; 2. Discuss with IEC on the proposed mitigation measures; 3. Make agreement on mitigation measures to be implemented; 4. Ensure mitigation measures are properly implemented. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Discuss with ET and IEC on possible remedial actions and propose mitigation measures to IEC and ER; 5. Implement the agreed mitigation measures. 6. Amend working methods if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
Action level being exceeded by two or more consecutive sampling days	<ol style="list-style-type: none"> 1. Repeat <i>in situ</i> measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, Contractor and ER; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Action level; 8. Repeat measurement on next day of exceedance to confirm findings. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; 4. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of non-compliance in writing; 2. Discuss with IEC on the proposed mitigation measures; 3. Make agreement on mitigation measures to be implemented; 4. Ensure mitigation measures are properly implemented; 5. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the Engineer and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Discuss with ET and IEC on possible remedial actions and propose mitigation measures to IEC and ER within 3 working days of notification; 5. Implement the agreed mitigation measures; 6. Amend working methods if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
Limit level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat <i>in-situ</i> measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, Contractor, ER and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit level. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; 4. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 3. Request Contractor to critically review the working methods; 4. Ensure mitigation measures are properly implemented; 5. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Submit proposal of mitigation measures to ER within 3 working days of notification and discuss with ET, IEC and ER; 5. Implement the agreed mitigation measures; 6. Amend working methods if appropriate.

Event	Action			
	ET Leader	IEC	ER	Contractor
Limit level being exceeded by two or more consecutive sampling days	<ol style="list-style-type: none"> 1. Repeat <i>in-situ</i> measurement to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, contractor, ER and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the Contractor's mitigation measures whenever necessary to assure their effectiveness and advise the ER accordingly. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 3. Request Contractor to critically review the working methods; 4. Make agreement on the mitigation measures to be implemented; 5. Ensure mitigation measures are properly implemented; 6. Assess the effectiveness of the implemented mitigation measures; 7. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Take immediate action to avoid further exceedance; 3. Rectify unacceptable practice; 4. Check all plant and equipment and consider changes of working methods; 5. Submit proposal of mitigation measures to ER within 3 working days of notification and discuss with ET, IEC and ER; 6. Implement the agreed mitigation measures; 7. Resubmit proposals of mitigation measures if problem still not under control; 8. As directed by the Engineer, to slow down or to stop all or part of the construction activities until no exceedance of Limit level.

Event / Action Plan for Dolphin Monitoring

Event	ET Leader	IEC	ER / SOR	Contractor
Action Level	<ol style="list-style-type: none"> 1. Repeat statistical data analysis to confirm findings; 2. Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences; 3. Identify source(s) of impact; 4. Inform the IEC, ER/SOR and Contractor; 5. Check monitoring data. 6. Review to ensure all the dolphin protective measures are fully and properly implemented and advise on additional measures if necessary. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor; 2. Discuss monitoring results and finding with the ET and the Contractor. 	<ol style="list-style-type: none"> 1. Discuss monitoring with the IEC and any other measures proposed by the ET; 2. If ER/SOR is satisfied with the proposal of any other measures, ER/SOR to signify the agreement in writing on the measures to be implemented. 	<ol style="list-style-type: none"> 1. Inform the ER/SOR and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the ER/SOR; 3. Implement the agreed measures.
Limit Level	<ol style="list-style-type: none"> 1. Repeat statistical data analysis to confirm findings; 2. Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences; 3. Identify source(s) of impact; 4. Inform the IEC, ER/SOR and Contractor of findings; 5. Check monitoring data; 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor; 2. Discuss monitoring results and findings with the ET and the Contractor; 3. Attend the meeting to discuss with ET, ER/SOR and Contractor the necessity of additional dolphin monitoring and any other potential mitigation measures. 4. Review proposals for additional monitoring and any other mitigation measures submitted 	<ol style="list-style-type: none"> 1. Attend the meeting to discuss with ET, IEC and Contractor the necessity of additional dolphin monitoring and any other potential mitigation measures. 2. If ER/SOR is satisfied with the proposals for additional dolphin monitoring and/or any other mitigation measures submitted by ET and Contractor and verified by IEC, ER/SOR to signify the agreement in writing on such proposals and any other mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER/SOR and confirm notification of the non-compliance in writing; 2. Attend the meeting to discuss with ET, IEC and ER/SOR the necessity of additional dolphin monitoring and any other potential mitigation measures. 3. Jointly submit with ET to IEC a proposal of additional dolphin monitoring and/or any other mitigation measures when necessary. 4. Implement the agreed additional dolphin monitoring

	<p>6. Repeat review to ensure all the dolphin protective measures are fully and properly implemented and advise on additional measures if necessary.</p> <p>7. If ET proves that the source of impact is caused by any of the construction activity by the works contract, ET to arrange a meeting to discuss with IEC, ER/SOR and Contractor the necessity of additional dolphin monitoring and/or any other potential mitigation measures (e.g., consider to modify the perimeter silt curtain or consider to control/temporarily stop relevant construction activity etc.) and submit to IEC a proposal of additional dolphin monitoring and/or mitigation measures where necessary.</p>	<p>by ET and Contractor and advise ER/SOR of the results and findings accordingly.</p> <p>5. Supervise / Audit the implementation of additional monitoring and/or any other mitigation measures and advise ER/SOR the results and findings accordingly.</p>	<p>3. Supervise the implementation of additional monitoring and/or any other mitigation measures.</p>	<p>and/or any other mitigation measures.</p>
--	---	---	---	--



China Harbour Engineering Company Limited

Monthly Summary Waste Flow Table for May / 2014 (year)

Project : Hong Kong – Zhuhai – Macao Bridge, Hong Kong Boundary Crossing Facilities – Reclamation Works

Contract No.: HY/2010/02

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete (see Note 1)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste (see Note 4)	Others, e.g. general refuse (see Note 3)
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 m ³)
Jan-14	0.0000	0.0000	0.0000	0.0000	0.0000	1158.9828	0.0000	0.1680	0.0000	2.0000	0.0325
Feb-14	0.0000	0.0000	0.0000	0.0000	0.0000	1064.5957	0.0000	0.2520	0.0000	0.0000	0.0520
Mar-14	0.0000	0.0000	0.0000	0.0000	0.0000	1111.9982	0.0000	0.0000	0.0000	1.4000	0.1690
Apr-14	0.0000	0.0000	0.0000	0.0000	0.0000	1294.8080	0.0000	0.0000	0.0000	0.0000	0.0845
May-14	0.0000	0.0000	0.0000	0.0000	0.0000	1181.4168	0.0400	0.0240	0.0000	1.0000	0.0910
Jun-14											
Sub-total	0.0000	0.0000	0.0000	0.0000	0.0000	5811.8015	0.0400	0.4440	0.0000	4.4000	0.4290
Jul-14											
Aug-14											
Sep-14											
Oct-14											
Nov-14											
Dec-14											
Total	0.0000	0.0000	0.0000	0.0000	0.0000	5811.8015	0.0400	0.4440	0.0000	4.4000	0.4290

- Notes:
- (1) Broken concrete for recycling into aggregates.
 - (2) Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging materials.
 - (3) Use the conversion factor : 1 full load of dumping truck being equivalent to 6.5m³ by volume.
 - (4) Chemical waste refer to spent “battery” and “oil with water”.

Appendix N

Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions

Cumulative statistics on Exceedances

		Total no. recorded in this month	Total no. recorded since project commencement
1-Hour TSP	Action	-	-
	Limit	-	-
24-Hour TSP	Action	-	-
	Limit	-	-
Noise	Action	-	-
	Limit	-	-
Water Quality	Action	-	1
	Limit	-	1
Dolphin Monitoring	Action	-	-
	Limit	-	-

Remarks: Exceedances which are not project-related are not presented in this table.

Cumulative statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions

	Date Received	Subject	Status	Total no. received in this month	Total no. received since project commencement
Environmental complaints	7 May 14	As informed by the Contractor on 7 May 14, a complaint was received by the Contractor on 17 April 14 concerning sand and dust emission from uncovered barges parking at the sea area off the Tuen Mun Ferry Pier. Investigation result shows that the complaint is unlikely to be related to this Contract.	Closed	1	19

	30 May 14	As informed by the Contractor on 30 May 14, an environmental complaint had been received on 28 May 2014. The complainant mentioned that waste such as earth and concrete were being felled into the sea everyday at the Hong Kong-Zhuhai-Macao Bridge at location where construction works are being conducted, causing pollution to the marine environment. After investigation, it is concluded that the complaint is unlikely to be related to this Contract.	Closed	2	20
Notification of summons	-	-	-	-	2
Successful Prosecutions	-	-	-	-	2
