


ASB Biodiesel (Hong Kong) Limited

Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate

Quarterly EM&A Report

April – June 2016

(Version 1.0)

Certified By 

(Environmental Team Leader)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

CINOTECH CONSULTANTS LTD

Room 1710, Technology Park,

18 On Lai Street,

Shatin, NT, Hong Kong

Tel: (852) 2151 2083 Fax: (852) 3107 1388

Email: info@cinotech.com.hk



MANNINGS
(Asia) Consultants Limited

Address: 5/F, Winning Commercial Building, 46-48 Hillwood Road, Tsim Sha Tsui, Kowloon
Tel: 852 - 3168 2028 Fax: 852 - 3168 2022

<i>To:</i>	Cinotech	<i>Date:</i>	19 September 2016
<i>Attn:</i>	Mr. H. T. Lai	<i>Fax:</i>	3107 1388
<i>From:</i>	Mr. Mark Cheung	<i>Ref:</i>	D1067/L05979
<i>Job No.</i>	D1067	<i>Total Pages:</i>	1

**Subject: Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate
Quarterly EM&A Report (April - June 2016)**

Dear Sir,

We refer to your submission of the Quarterly EM&A Report for April 2016 to June 2016 via email dated 5 September 2016.

We write to advise that we have no comment on the captioned report.

However, it is noted that there was incidents of exceedance of limit level during the report period. Please make sure the appropriate remedial measures are promptly implemented and and keep tracking on the effectiveness of the proposed remedial measures.

Regards,

Mark Cheung
Independent Environmental Checker

KTC/gk

TABLE OF CONTENTS

	Page
EXECUTIVE SUMMARY	1
Introduction	1
Environmental Licenses and Permits	1
Environmental Monitoring and Audit Works	1
Key Information in the Reporting Month	1
1 INTRODUCTION	2
Background	2
Project Organizations	2
Summary of EM&A Requirements	3
Status of Environmental Licensing and Permitting	3
2 ENVIRONMENTAL MONITORING REQUIREMENTS	4
Air Quality	4
Water Quality	4
Sulphur Content in Bio Heating Oil	4
3 MONITORING RESULTS	5
Air Quality	5
Water Quality	7
Sulphur Content in Bio Heating Oil	8
Summary of Exceedance Events in the Reporting Quarter	9
4 SUMMARY OF COMPLAINT AND PROSECUTION	10
5 CONCLUSIONS	11

LIST OF TABLES

Table I	Summary of Key Information in April – June 2016
Table 1-1	Key Project Contacts
Table 3-1	Monitoring Result of the Emission from the Stack of Boiler
Table 3-2	Monitoring Result of the Emission from the Stack of Biogas Flare
Table 3-3	Monitoring Result of the Emission from the Stack of Process Building
Table 3-4	Monitoring Result of the Odour Concentrations at the Final Air Scrubber
Table 3-5	Monitoring Result of Odour Patrols along Site Boundary
Table 3-6	Water Quality Monitoring Result of Treated Effluent Discharged from Project Site
Table 3-7	Water Quality Monitoring Result of Stormwater Discharge
Table 3-8	Monitoring Result of Sulphur Content in Bio Heating Oil
Table 3-9	Summary of Exceedance Events in the Reporting Quarter

LIST OF FIGURES

Figure 1.1	Location Plan
------------	---------------

LIST OF APPENDICES

Appendix A	Summary of Environmental Licensing and Permit Status
Appendix B	Summary of Monitoring Criteria
Appendix C	Event and Action Plan
Appendix D	Graphical Presentation of Monitoring Results – Air Quality
Appendix E	Graphical Presentation of Monitoring Results – Water Quality
Appendix F	Graphical Presentation of Monitoring Results – Sulphur Content in Bio Heating Oil
Appendix G	Exceedance Report
Appendix H	Complaint Log

EXECUTIVE SUMMARY

Introduction

1. This is the 1st quarterly Environmental Monitoring and Audit (EM&A) Report prepared by Cinotech Consultants Limited for Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate in operational phase. This report documents the findings of EM&A works carried out in April – June 2016.

Environmental Licenses and Permits

2. Licenses/Permits granted to the Project include the followings:
 - Environmental Permit, EP-319/2009/D, granted on 28 January 2014;
 - Specified Process Licence, L-25-019(1), granted on 10 October 2013 &
 - Water Pollution Control Ordinance Licence, WT00022972-2015, granted on 16 December 2015.

Environmental Monitoring and Audit Works

3. Environmental monitoring and audit works for the Project were carried out in accordance with the criteria and requirements listed in the EM&A Manual, Environmental Permit, Specified Process Licence and Water Pollution Control Ordinance (WPCO) Licence granted. Monitoring results were checked and reviewed.

Key Information in the Reporting Month

4. Summary of key information in this reporting quarter (April – June 2016) is listed in **Table I**.

Table I Summary of Key Information in April – June 2016

Event	Event Details		Action Taken	Status	Remark
	Number	Nature			
Exceedance of Action & Limit Levels	6	---	Exceedance events were investigated and measures have been proposed.	---	---
Complaint received	0	---	N/A	N/A	---
Changes to the assumptions and key construction / operation activities recorded	0	---	N/A	N/A	---
Status of submissions under EP	1	Monthly EM&A Reports for April 2016	Submitted to EPD on 3 June 2016	Verified by IEC	---
Notifications of any summons & prosecutions	0	---	N/A	N/A	---

1 INTRODUCTION

Background

- 1.1 Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate (hereafter referred to as “the Project”) is to construct and operate a 100,000 tonnes per annum biodiesel plant at Tseung Kwan O Industrial Estate (see **Figure 1.1** for the location plan of Project Site). The plant will use a multi-feedstock which consists of used cooking oil (UCO), oil and grease recovered from grease trap waste (GTW), palm fatty acid distillate (PFAD) and animal fats. The proposed biodiesel plant offers a convenient recycling outlet for GTW and UCO, and converts oil and grease recovered from these wastes into useful products. The Project also offers a more environmental-friendly alternative to the diesel fuel market in Hong Kong.
- 1.2 This Project is a Designated Project under the Environmental Impact Assessment Ordinance (Cap. 499). An environmental impact assessment (EIA) was undertaken to identify and evaluate the impact on environment (e.g. air quality, noise, water quality and ecology), and propose possible measures to mitigate the impact. The EIA Report was approved by the Environmental Protection Department (EPD) on 26 February 2009.
- 1.3 Environmental Permit (EP) No. EP-319/2009 was issued on 11 March 2009 to ASB Biodiesel (Hong Kong) Limited as the Permit Holder. After several rounds of amendments, the latest version is EP No. EP-319/2009/D, which was issued on 28 January 2014.
- 1.4 Construction of the Biodiesel Plant has been completed since October 2013. After more than 2 years of commissioning trial, the Plant started to operate in April 2016. Cinotech Consultants Limited was commissioned by ASB Biodiesel (Hong Kong) Limited to undertake the Environmental Monitoring and Audit (EM&A) works for the Project. This is the 1st Quarterly EM&A report summarizing the EM&A works in operational phase for the Project in April – June 2016.

Project Organizations

- 1.5 Different parties with different levels of involvement in the project organization include:
 - Project Proponent & Operator – ASB Biodiesel (Hong Kong) Limited
 - Independent Environmental Checker (IEC) – Mannings (Asia) Consultants Ltd.
 - Environmental Team (ET) – Cinotech Consultants Limited
- 1.6 The responsibilities of respective parties are detailed in Section 2 of the Final EM&A Manual of the Project.
- 1.7 The key contacts of the Project are shown in **Table 1-1**.

Table 1-1 Key Project Contacts

Party	Role	Name	Position	Phone No.
ASB	Permit Holder & Operator	Mr. Albert Kwan	Facilities and Operations Manager	3183 4209
		Ms. Fion Wong	Engineer	3183 4204
Mannings	Independent Environmental Checker	Mr. Mark Cheung	Independent Environmental Checker	3168 2028
		Mr. Gavin Kwok	Assistant to Independent Environmental Checker	3970 8628
Cinotech	Environmental Team	Dr. HF Chan	ET Leader	2151 2088
		Ms. Betty Choi	Project Coordinator	2151 2072

Summary of EM&A Requirements

- 1.8 EM&A requirements for the Project include:
- Monitoring requirements as listed in the Project EM&A Manual;
 - Conditions listed in the Environmental Permit; &
 - Conditions listed in the SP License.

Status of Environmental Licensing and Permitting

- 1.9 All permits/licenses obtained for the Project are summarized in **Appendix A**.

2 ENVIRONMENTAL MONITORING REQUIREMENTS

Air Quality

- 2.1 According to Section 4.3 of the Final EM&A Manual of the Project, the emission from stacks of boiler, biogas flare and process building, and odour concentrations at the final air scrubber shall be monitored. Odour patrols along the Project Site boundary is also required. Detailed monitoring criteria (i.e. frequency, parameter, and action & limit levels) are listed in **Appendix B**. If limit levels are exceeded, the event and action plan as shown in **Appendix C** should be implemented.

Water Quality

- 2.2 According to Section 6.3 of the Final EM&A Manual of the Project, the water quality of treated effluent discharged from Project Site and stormwater discharge shall be monitored. Detailed monitoring criteria (i.e. frequency, parameter, and limit levels) are listed in **Appendix B**. If limit levels are exceeded, the event and action plan as shown in **Appendix C** should be implemented.

Sulphur Content in Bio Heating Oil

- 2.3 According to Section 3.11 of the EP-319/2009/D, if Bio Heating Oil (BHO) is used on site, the sulphur content in BHO shall be monitored. Monitoring criteria (i.e. frequency, parameter, and limit level) for the sulphur content in BHO are listed in **Appendix B**. If limit level is exceeded, the following actions should be taken by the ET:
- Inform Project Proponent and IEC within 24 hours;
 - Inform Project Proponent to increase the use of low sulphur diesel in the fuel tank(s) to achieve a fuel mixture with sulphur content of less than 346 ppm; and
 - Revert the monitoring programme to the original frequency of a test for every tank load of BHO, or at such a monitoring frequency to be advised and agreed by the EPD's Director.

3 MONITORING RESULTS

Air Quality

Emission from Stack of Boiler

- 3.1 Emissions from stacks of boiler was sampled and analyzed monthly. Monitoring result of boiler emission in April – June 2016 is summarized in **Table 3-1** below and graphical presentation of results is shown in **Appendix D**.

Table 3-1 Monitoring Result of the Emission from the Stack of Boiler

Parameter	Limit Level	Monitoring Result *		
		Apr-16	May-16	Jun-16
Nitrogen oxides (NO _x)	2.213 kg/h	0.65 kg/h	1.59 kg/h	0.93 kg/h
Carbon monoxide (CO)	0.553 kg/h	< 0.2 kg/h	< 0.2 kg/h	0.789 kg/h ***
Sulphur dioxide (SO ₂)	0.797 kg/h	< 0.02 kg/h	< 0.03 kg/h	< 0.02 kg/h
Non-methane Organic Compounds (NMOC)	0.041 kg/h	0.0025 kg/h	0.0395 kg/h	0.0525 kg/h ***
Exhaust gas velocity	7 m/s **	12 m/s	16.125 m/s	11.5 m/s

* Average result of all trials is presented. If one of the data was smaller than the limit of reporting, the smallest recordable value would be used for calculation of average.
 ** Minimum level should be achieved.
 *** Value exceeded Limit Level.

- 3.2 Two exceedances of Limit Level were reported in June 2016. Investigation of the exceedance events was finished and measures were proposed for countering the exceedances.

Emission from Stack of Biogas Flare

- 3.3 Emissions from stacks of biogas flare was sampled and analyzed monthly. Summary of monitoring result of the emission from the stack of biogas flare in April – June 2016 is presented in **Table 3-2** below and graphical presentation of results is shown in **Appendix D**.

Table 3-2 Monitoring Result of the Emission from the Stack of Biogas Flare

Parameter	Limit Level	Monitoring Result *		
		Apr-16	May-16	Jun-16
Nitrogen oxides (NO _x)	0.053 kg/h	< 0.007 kg/h	< 0.005 kg/h	< 0.03 kg/h
Carbon monoxide (CO)	0.018 kg/h	< 0.009 kg/h	0.0515 kg/h***	0.092 kg/h***
Sulphur dioxide (SO ₂)	0.039 kg/h	< 0.003 kg/h	< 0.003 kg/h	< 0.01 kg/h
Non-methane Organic Compounds (NMOC)	0.0018 kg/h	0.0005 kg/h	0.00185 kg/h***	0.0036 kg/h***

Parameter	Limit Level	Monitoring Result *		
		Apr-16	May-16	Jun-16
Exhaust gas velocity	0.54 m/s **	1.2 m/s	1.4 m/s	4.45 m/s
* Average result of all trials is presented. If one of the data was smaller than the limit of reporting, the smallest recordable value would be used for calculation of average. ** Minimum level should be achieved. *** Value exceeded Limit Level.				

3.4 Two exceedances of Limit Level were reported in May 2016, and two exceedances of Limit Level were reported in June 2016. Investigation of the exceedance events was finished and measures were proposed for countering the exceedances.

Emission from Stack of Process Building

3.5 Emissions from stacks of process building was sampled and analyzed monthly. Summary of monitoring result of the emission from the stack of process building in April – June 2016 is presented in **Table 3-3** below and graphical presentation of results is shown in **Appendix D**.

Table 3-3 Monitoring Result of the Emission from the Stack of Process Building

Parameter	Limit Level	Monitoring Result *		
		Apr-16	May-16	Jun-16
Acetyldehyde	0.0975 kg/h	<0.001 kg/h	<0.001 kg/h	<0.001 kg/h
Methanol	0.0975 kg/h	<0.01 kg/h	0.015 kg/h	<0.01 kg/h
Exhaust gas velocity	0.79 m/s **	2.9 m/s	1.9 m/s	2 m/s
* Average result of all trials is presented. If one of the data was smaller than the limit of reporting, the smallest recordable value would be used for calculation of average. ** Minimum level should be achieved.				

3.6 No exceedance of Limit Level was reported in April – June 2016.

Odour Concentration at the Final Air Scrubber

3.7 Odour Concentration at the final air scrubber was sampled and analyzed monthly. Summary of monitoring result of odour concentrations at the final air scrubber in April – June 2016 is presented in **Table 3-4** below and graphical presentation of results is shown in **Appendix D**.

Table 3-4 Monitoring Result of the Odour Concentrations at the Final Air Scrubber

Parameter	Limit Level	Monitoring Result *		
		Apr-16	May-16	Jun-16
Odour	200.3 OU/s	13.5 OU/s	5.725 OU/s	14.5 OU/s
Exhaust gas velocity	0.7 m/s **	1.5 m/s	0.75 m/s	0.85 m/s
* Average result of all trials is presented. If one of the data was smaller than the limit of reporting, the smallest recordable value would be used for calculation of average. ** Minimum level should be achieved.				

3.8 No exceedance of Limit Level was reported in April – June 2016.

Odour Patrols along Site Boundary

3.9 Odour intensity were monthly monitored by the odour patrols. Odour patrols were carried out by a qualified odour panelist in both morning and afternoon on 21 April, 12 May and 6 June 2016. Summary of monitoring result of odour patrols in April – June 2016 is presented in **Table 3-5** below and graphical presentation of results is shown in **Appendix D**.

Table 3-5 Monitoring Result of Odour Patrols along Site Boundary

Date	Odour Intensity		
	Action Level	Limit Level	Range of Measured Level
April 2016	Odour intensity \geq Class 2 recorded	Odour intensity \geq Class 3 recorded on 2 consecutive patrols	0-1
May 2016			0-1
June 2016			0-1

3.10 No exceedance of Action and Limit Levels was reported in April – June 2016.

Water Quality

Water Quality of Treated Effluent Discharged from Project Site

3.11 Water quality of treated effluent discharged from Project Site was sampled and analyzed monthly. Summary of water quality monitoring result of treated effluent discharge from Project Site in April – June 2016 is presented in **Table 3-6** below and graphical presentation of results is shown in **Appendix E**.

Table 3-6 Water Quality Monitoring Result of Treated Effluent Discharged from Project Site

Parameter	Limit Level	Monitoring Result		
		Apr-16	May-16	Jun-16
pH	Within the range of 6-10	8.1	7.73	8.07
Suspended Solids	800 mg/L	678 mg/L	760 mg/L	149 mg/L
Biochemical Oxygen Demand (BOD) (5 days, 20°C)	800 mg/L	436 mg/L	779 mg/L	256 mg/L
Chemical Oxygen Demand (COD)	2000 mg/L	1534 mg/L	1800 mg/L	418 mg/L

Parameter	Limit Level	Monitoring Result		
		Apr-16	May-16	Jun-16
Oil & Grease	50 mg/L	31 mg/L	42 mg/L	<10 mg/L
Sulphate	1000 mg/L	640 mg/L	10 mg/L	10 mg/L
Total Nitrogen	200 mg/L	176 mg/L	160 mg/L	160 mg/L
Total Phosphorus	50 mg/L	41 mg/L	44 mg/L	25 mg/L

3.12 No exceedance of Limit Level was reported in April – June 2016.

Water Quality of Stormwater Discharge

3.13 Water quality of stormwater discharge was sampled and analyzed quarterly. Summary of water quality monitoring result of stormwater discharge in April – June 2016 is presented in **Table 3-7** below and graphical presentation of results is shown in **Appendix E**.

Table 3-7 Water Quality Monitoring Result of Stormwater Discharge

Parameter	Limit Level	Monitoring Result		
		Apr-16	May-16	Jun-16
pH	Within the range of 6-9	--	--	7.01
Suspended Solids	50 mg/L	--	--	40 mg/L
Biochemical Oxygen Demand (BOD) (5 days, 20°C)	50 mg/L	--	--	48 mg/L
Chemical Oxygen Demand (COD)	100 mg/L	--	--	56 mg/L
Oil & Grease	30 mg/L	--	--	<10 mg/L

* Water quality of stormwater discharge from Project Site was sampled and analyzed quarterly

3.14 No exceedance of Limit Level was reported in April – June 2016.

Sulphur Content in Bio Heating Oil

3.15 Sulphur content in bio heating oil was sampled and analyzed every tank load of the bio heating oil when the fuel tank(s) is being filled/refilled. Summary of monitoring result of Sulphur content in bio heating oil in April – June 2016 is presented in **Table 3-8** below and graphical presentation of results is shown in **Appendix F**.

Table 3-8 Monitoring Result of Sulphur Content in Bio Heating Oil

Parameter	Limit Level	Monitoring Result		
		Apr-16	May-16	Jun-16
Sulphur Content	346 ppm	296 ppm	335 ppm	338 ppm

3.16 No exceedance of Limit Level was reported in April – June 2016.

Summary of Exceedance Events in the Reporting Quarter

3.17 A summary of all exceedance events is presented in **Table 3-9** below. Investigation reports for the exceedances in May 2016 and June 2016 are attached in the Monthly EM&A Reports (May and June 2016) respectively.

Table 3-9 Summary of Exceedance Events in the Reporting Quarter

Parameter		Unit	Limit Level *	Monitoring Result
April 2016				
Nil.		--	--	--
May 2016				
Stack of Biogas Flare	Carbon monoxide (CO)	kg/h	0.018	0.0515
	Non-methane Organic Compounds (NMOC)	kg/h	0.001764	0.00185
June 2016				
Stack of Boiler	Carbon monoxide (CO)	kg/h	0.612	0.789
	Non-methane Organic Compounds (NMOC)	kg/h	0.04068	0.0525
Stack of Biogas Flare	Carbon monoxide (CO)	kg/h	0.018	0.092
	Non-methane Organic Compounds (NMOC)	kg/h	0.001764	0.0036

* No action level was set in the Final EM&A Manual of the Project and in the Specified Process Licence

4 SUMMARY OF COMPLAINT AND PROSECUTION

- 4.1 No environmental related complaint, prosecution or notification of summon was received in April – June 2016.
- 4.2 There was no environmental complaint, prosecution or notification of summons received since the commencement of Project (operational phase). The Complaint Log is attached in **Appendix H**.

5 CONCLUSIONS


- 5.1 In April – June 2016, environmental monitoring and audit works were carried out in accordance with criteria and requirements listed in the Project EM&A Manual, Environmental Permit EP-319/2009D, Specified Process Licence L-25-019(1) and Water Pollution Control Ordinance Licence WT00022972-2015.
- 5.2 Monitoring of air quality, water quality and sulphur content in Bio Heating Oil were carried out at designated locations. 2 exceedances of Limit Levels were recorded at the stack of boiler, and 4 exceedances of Limit Levels were recorded at the stack of biogas flare in the reporting quarter. Investigation reports for the exceedances in May 2016 and June 2016 are attached in the Monthly EM&A Reports (May and June 2016) respectively.
- 5.3 No environmental related complaint, prosecution or notification of summon was received.

FIGURES



Key 圖例

 Proposed Site



Meters 米

0 100 200 400



Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate

Location Plan

Scale

N.T.S

Date

MAY 2016

Project

No.

MA15052

Figure

1.1

CINOTECH

APPENDIX A
Summary of Environmental Licensing and
Permit Status

Appendix A Summary of Environmental Licensing and Permit Status

Permit / License No.	Valid Period		Summary	Status
	From	To		
Environmental Permit (EP)				
EP-319/2009/D	28/01/2014	N/A	Operation of <ul style="list-style-type: none"> • a biochemical plant with a storage capacity of more than 500 tonnes and in which substances are processed and produced; • a storage, transfer and transshipment of oil facility with a storage capacity of not less than 1,000 tonnes; and • a dangerous goods godown with a storage capacity exceeding 500 tonnes 	Valid
Specified Process (SP) Licence				
L-25-016(1)	10/10/2013	10/10/2015	<ul style="list-style-type: none"> • Emission of non-fugitive fixed point emissions 	Under renewal
Water Pollution Control Ordinance (WPCO) Licence				
WT00022972-2015	16/12/2015	31/12/2017	Discharge of <ul style="list-style-type: none"> • effluent from wastewater treatment facilities to communal foul sewer; and • effluent from floor washing of operation areas to communal storm drain 	Valid

APPENDIX B
Summary of Monitoring Criteria

Appendix B Summary of Monitoring Criteria

Air Quality				
	Frequency	Parameter	Action Levels	Limit Levels
Emission from Stack of Boiler (EP2)	Monthly for the first 12 months of operation. If the monitoring results of the first year monitoring meet the limit level, the monitoring will be reduced to half-yearly intervals for the whole operational stage. *	Nitrogen oxides (NO _x)	– **	2.213 kg/h
Emission from Stack of Biogas Flare (EP1)		Carbon monoxide (CO)		0.553 kg/h
Emission from Stack of Process Building (EP3)		Sulphur dioxide (SO ₂)		0.797 kg/h
		Non-methane Organic Compounds (NMOC)		0.041 kg/h
		Exhaust gas velocity		7 m/s (minimum)
		NO _x	– **	0.053 kg/h
		CO		0.018 kg/h
		SO ₂		0.039 kg/h
		NMOC		0.0018 kg/h
		Exhaust gas velocity		0.54 m/s (minimum)
		Acetyldehyde	– **	0.0975 kg/h
		Methanol		0.0975 kg/h
		Exhaust gas velocity		0.79 m/s (minimum)
Odour Concentrations at the Final Air Scrubber (EP5)	Monthly for the first 2 years of operation *	Odour	– **	200.3 OU/s
		Exhaust gas velocity		0.7 m/s (minimum)
Odour Patrols along the Project Site Boundary	<p>Two times a day, one in the morning and one in the afternoon</p> <ul style="list-style-type: none"> Monthly for the first 12 months of operation. If the monitoring results of the first year monitoring meet the limit level, the monitoring frequency will be reduced to quarterly intervals in the second year; If the action level is triggered during the second year of operation, the frequency will be resumed to monthly intervals until compliance with the action level for three consecutive months is obtained; If the action level is not triggered for four consecutive quarterly monitoring, the monitoring can be terminated. 	Odour Intensity	<ul style="list-style-type: none"> Odour intensity \geq Class 2 recorded; or One documented complaint received 	<ul style="list-style-type: none"> Odour intensity \geq Class 3 recorded on 2 consecutive patrols
<p>* Monitoring will not be carried out during raining days</p> <p>** No action level is set in the Final EM&A Manual of the Project and in the Specified Process Licence</p>				

Appendix B Summary of Monitoring Criteria

Water Quality			
Discharge	Frequency	Parameter	Limit Levels
Treated Effluent Discharged from Project Site	Monthly	pH	Within the range of 6 - 10
		Suspended Solids	800 mg/L
		Biochemical Oxygen Demand (BOD) (5 days, 20 °C)	800 mg/L
		Chemical Oxygen Demand (COD)	2000 mg/L
		Oil & Grease	50 mg/L
		Sulphate	1000 mg/L
		Total Nitrogen	200 mg/L
		Total Phosphorus	50 mg/L
Stormwater Discharge	Quarterly	pH	Within the range of 6 – 9
		Suspended Solids	50 mg/L
		Biochemical Oxygen Demand (BOD) (5 days, 20 °C)	50 mg/L
		Chemical Oxygen Demand (COD)	100 mg/L
		Oil & Grease	30 mg/L

* No action level was set in the WPCO Licence

Appendix B Summary of Monitoring Criteria

Sulphur Content in Bio Heating Oil		
Frequency	Parameter	Limit Levels
<p>Every tank load of the BHO for the BHO's sulphur content when the fuel tank(s) is being filled/refilled</p> <ul style="list-style-type: none"> • This original frequency shall be adopted in the first three months of using BHO on site. After the first three months of the original monitoring regime, if all monitoring result in the first three months meet the limit level, the frequency may be reduced to one test for every two refills for the next three months; and after the first six months, the monitoring may be conducted once a month. • If exceedance occur, the monitoring shall be reverted to the original frequency of a test for every tank load of BHO, or at such a monitoring frequency to be advised and agreed by the EPD's Director. 	Sulphur Content	346 ppm
* No action level was set in the EP of the Project		

APPENDIX C
Event and Action Plan

Appendix C Event and Action Plan

Air Quality			
Event	Actions		
	ET Leader	IEC	Project Proponent
Exceedance of Limit Level for stack emission from boiler, biogas flare, process building and final air scrubber	<ul style="list-style-type: none"> • Inform Project Proponent and IEC, and investigate and record the cause of exceedance within 24 hours • Repeat measurement to confirm finding • Identify source(s) and investigate the cause(s) of exceedance • Inform Project Proponent whether the cause of exceedance is due to the Project • Prepare the Notification of Exceedance within 24 hours • Discuss remedial actions with the Project Proponent • Assess the effectiveness of Project Proponent's remedial actions • For the monitoring of emissions from the stacks of the boiler, biogas flare and process building, increase the monitoring frequency from half-yearly (for the second year onward) to monthly intervals. If results of three consecutive monthly monitoring show no exceedance of the limit level, the monitoring frequency will be reverted back to half-yearly intervals. 	<ul style="list-style-type: none"> • Verify the Notification of Exceedance submitted by the ET Leader • Check with the Project Proponent on the operating activities and implementation of control measures • Discuss with ET Leader and Project Proponent on the possible remedial actions • Advise the Project Proponent on the effectiveness of the proposed remedial measures • Supervise implementation of remedial measures 	<ul style="list-style-type: none"> • Rectify any unacceptable practice • Amend working methods as required • Implement amended working methods, if necessary
Exceedance of Action Level for odour	<ul style="list-style-type: none"> • Inform Project Proponent and IEC, and investigate and record the cause of exceedance within 24 hours • Repeat measurement to confirm finding • Identify source(s) / reason of exceedance or complain • Prepare the odour complain form or the Notification of Exceedance within 24 hours • Inform Project Proponent whether the cause of exceedance is due to the Project • Discuss remedial actions with the Project Proponent • During the second year of operation, if the action level is triggered, the frequency will be resumed to monthly until compliance with the action level for three consecutive months is obtained and the frequency will be reduced to quarterly intervals thereafter. 	<ul style="list-style-type: none"> • Verify the Notification of Exceedance submitted by the ET Leader 	<ul style="list-style-type: none"> • Rectify any unacceptable practice • Amend working methods as required • Implement amended working methods, if necessary





Appendix C Event and Action Plan

<p>Exceedance of Limit Level for odour</p>	<ul style="list-style-type: none"> • Inform Project Proponent and IEC, and investigate and record the cause of exceedance within 24 hours • Repeat measurement to confirm finding • Identify source(s) / reason of exceedance or complain • Prepare the odour complain form or the Notification of Exceedance within 24 hours • Inform Project Proponent whether the cause of exceedance is due to the Project • Assess the effectiveness of Project Proponent's remedial actions or amended design 	<ul style="list-style-type: none"> • Verify the Notification of Exceedance submitted by the ET Leader • Check with the Project Proponent on the operating activities and implementation of control measures • Discuss with ET Leader and Project Proponent on the possible remedial actions • Advise the Project Proponent on the effectiveness of the proposed remedial measures • Supervise implementation of remedial measures 	<ul style="list-style-type: none"> • Rectify any unacceptable practice • Propose and implement remedial measures or amend design as required within 3 working days of notification • Resubmit proposals if problem still not under control
--	---	--	---


Appendix C Event and Action Plan

Water Quality			
Event	Actions		
	ET Leader	IEC	Project Proponent
Exceedance of Limit Level for Treated Effluent Discharged from Project Site	<ul style="list-style-type: none"> • Inform Project Proponent and IEC, and investigate and record the cause of exceedance within 24 hours • Repeat measurement to confirm finding • Identify source(s) and investigate the cause(s) of exceedance • Prepare the Notification of Exceedance within 24 hours • Discuss remedial actions with the Project Proponent • Assess the effectiveness of Project Proponent's remedial actions 	<ul style="list-style-type: none"> • Verify the Notification of Exceedance submitted by the ET Leader • Check with Contractor on the operating activities and implementation of landfill gas control measures • Discuss with ET Leader and Contractor on the possible remedial actions • Advise the IC on the effectiveness of the proposed remedial measures • Supervise implementation of remedial measures 	<ul style="list-style-type: none"> • Check the performance of the on-site WWTP • Rectify any unacceptable performance • Carry out remedial measures or amend design as required • Implement amended design, if necessary
Exceedance of Limit Level for Stormwater Discharged from the Project Site	<ul style="list-style-type: none"> • Inform Project Proponent and IEC, and investigate and record the cause of exceedance within 24 hours • Repeat measurement to confirm finding • Identify source(s) and investigate the cause(s) of exceedance • Prepare the Notification of Exceedance within 24 hours • Discuss remedial actions with the Project Proponent • Assess the effectiveness of Project Proponent's remedial actions 	<ul style="list-style-type: none"> • Verify the Notification of Exceedance submitted by the ET Leader • Check with Project Proponent on the operating activities • Discuss with ET Leader and Project Proponent on the possible remedial actions • Advise the Project Proponent on the effectiveness of the proposed remedial measures • Supervise implementation of remedial measures 	<ul style="list-style-type: none"> • Propose and implement remedial measures or amend design as required • Rectify any unacceptable practice • Amend working methods as required • Implement amended working methods, if necessary





APPENDIX D
Graphical Presentation of Monitoring
Results – Air Quality

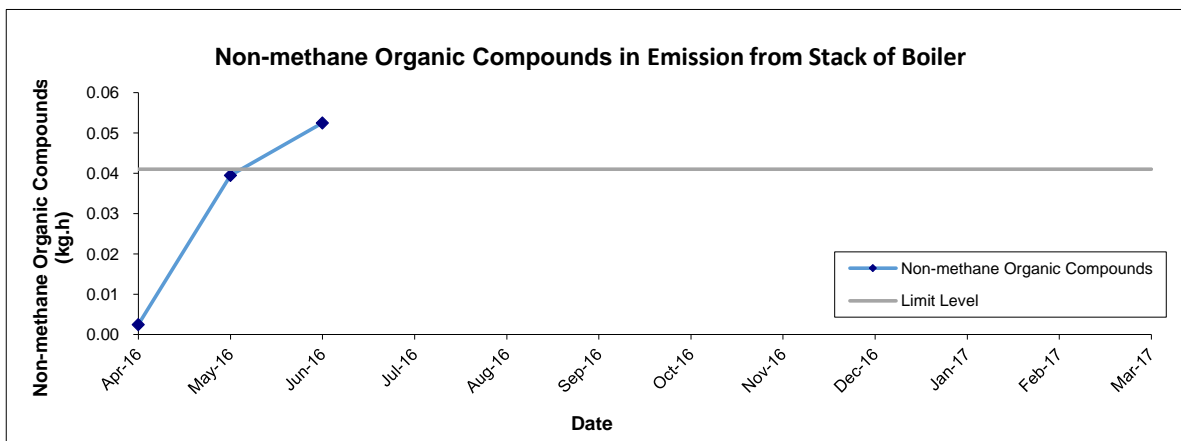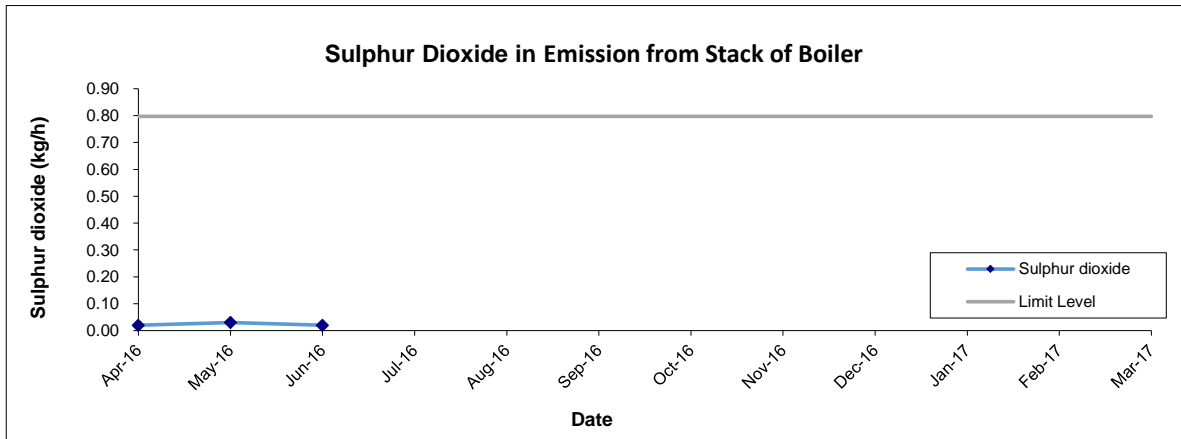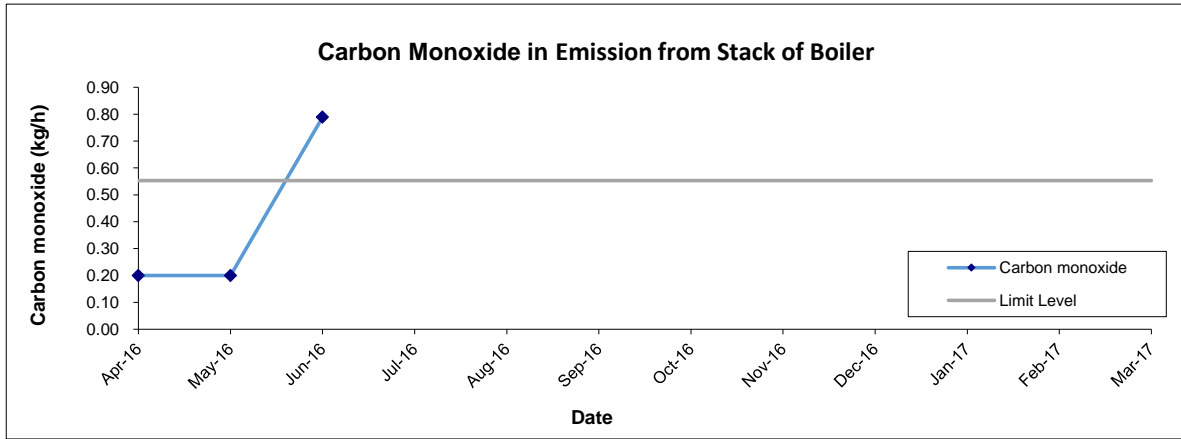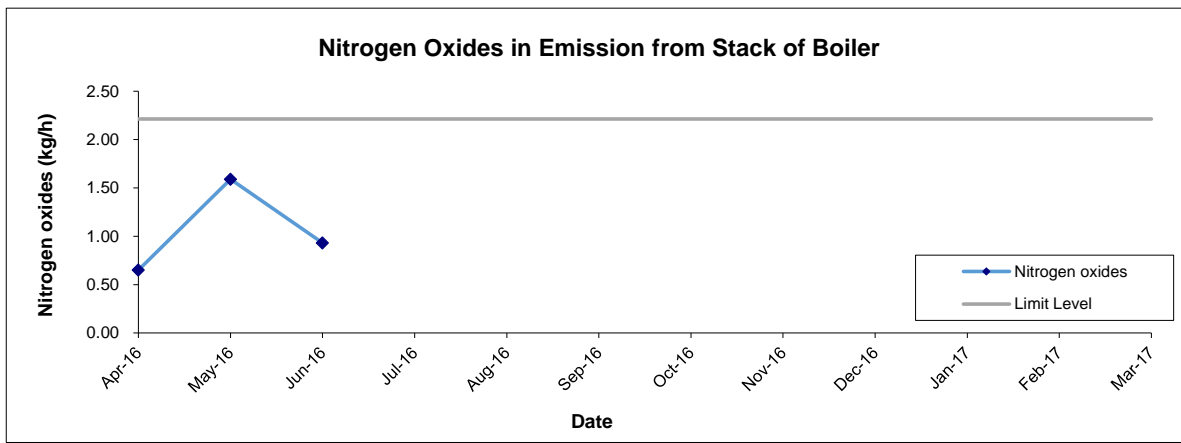


Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Air Quality (Emission from Stack of Boiler)	Scale	N.T.S	Project No. MA15052	CINOTECH
	Date	Jul 16	Appendix D-1	

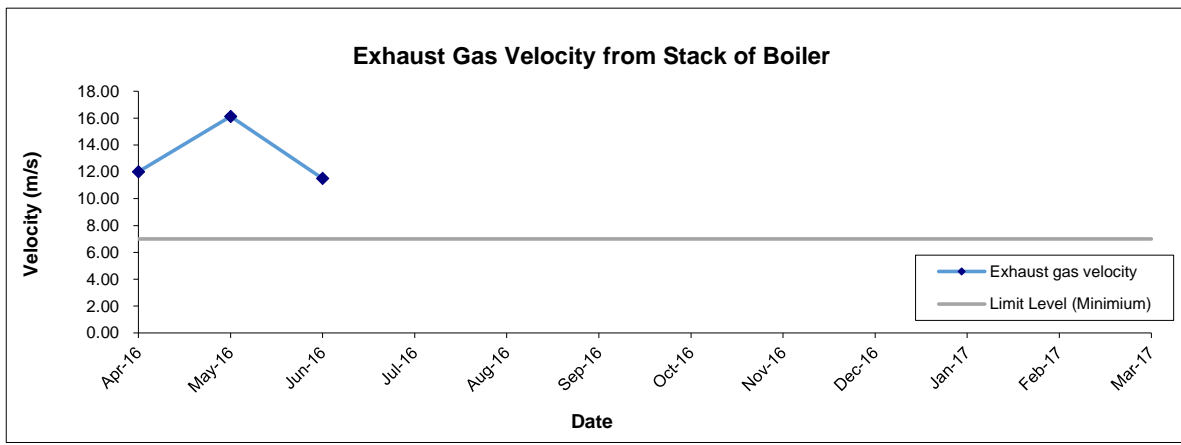




Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Air Quality (Emission from Stack of Boiler)	Scale N.T.S	Project No. MA15052	CINOTECH
	Date Jul 16	Appendix D-2	

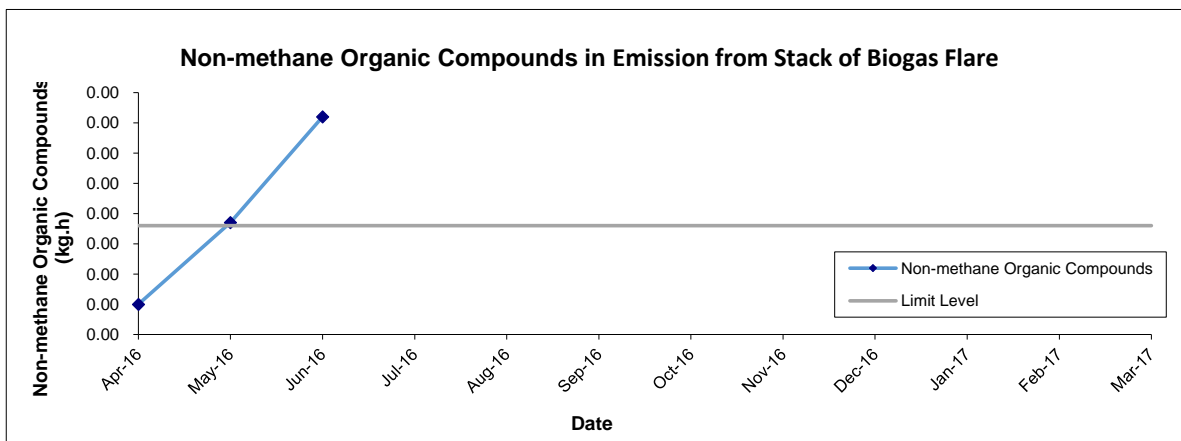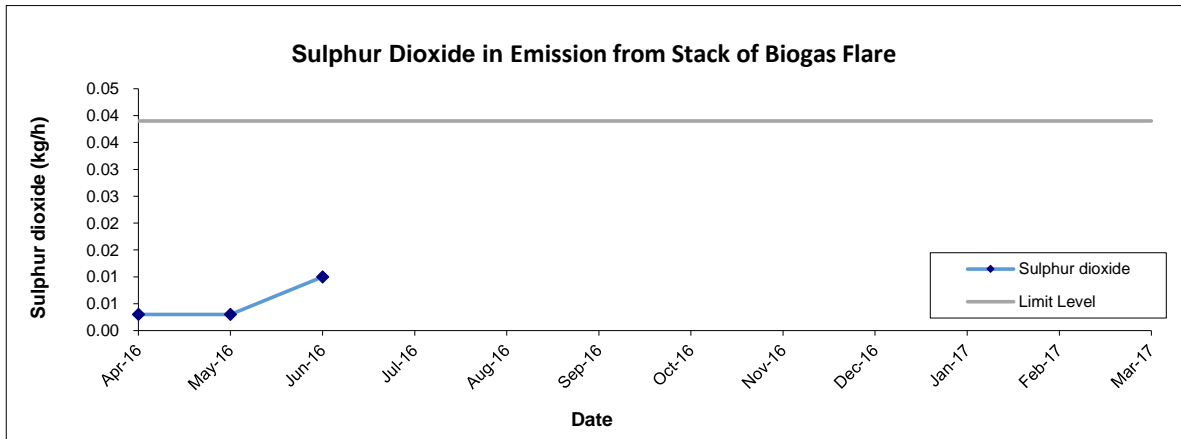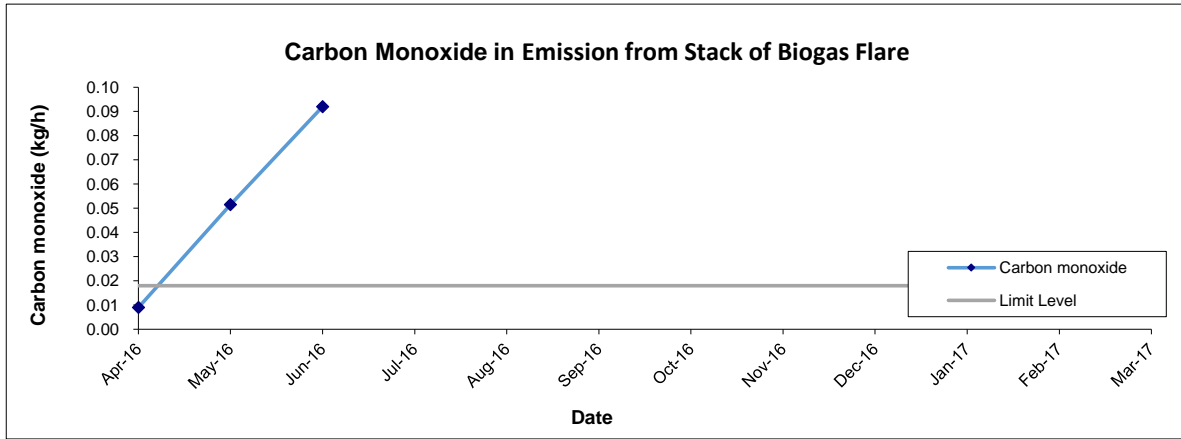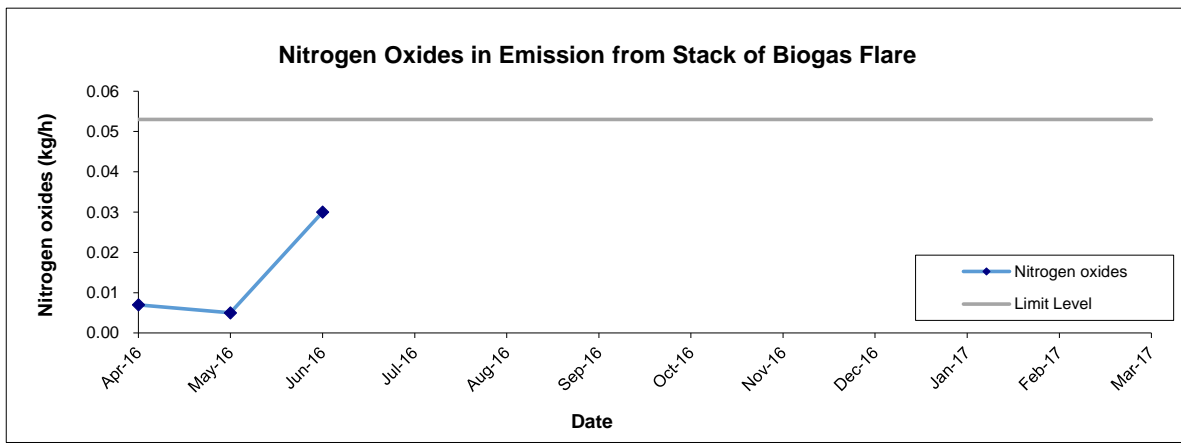



Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Air Quality (Emission from Stack of Biogas Flare)	Scale	N.T.S	Project No.	MA15052	CINOTECH
	Date	Jul 16	Appendix	D-3	

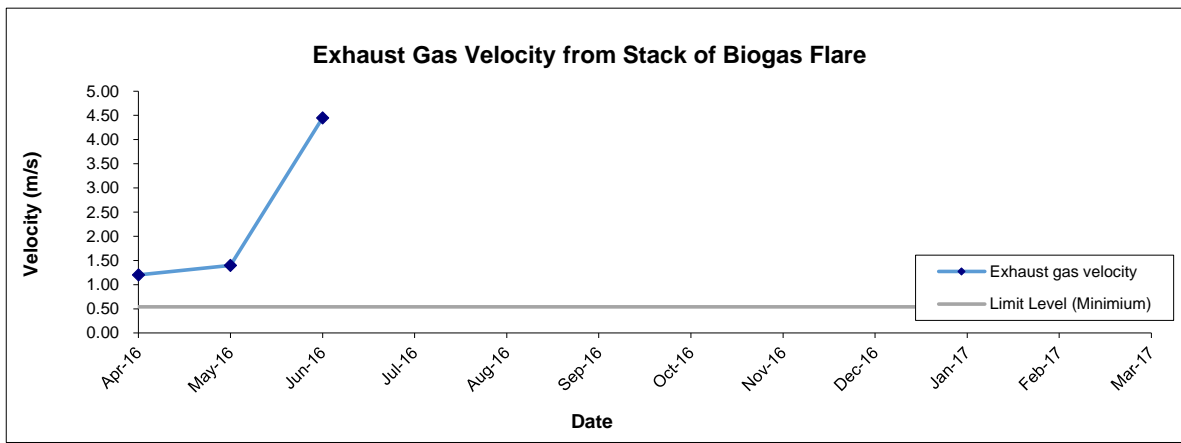


Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Air Quality (Emission from Stack of Biogas Flare)	Scale N.T.S	Project No. MA15052	
	Date Jul 16	Appendix D-4	

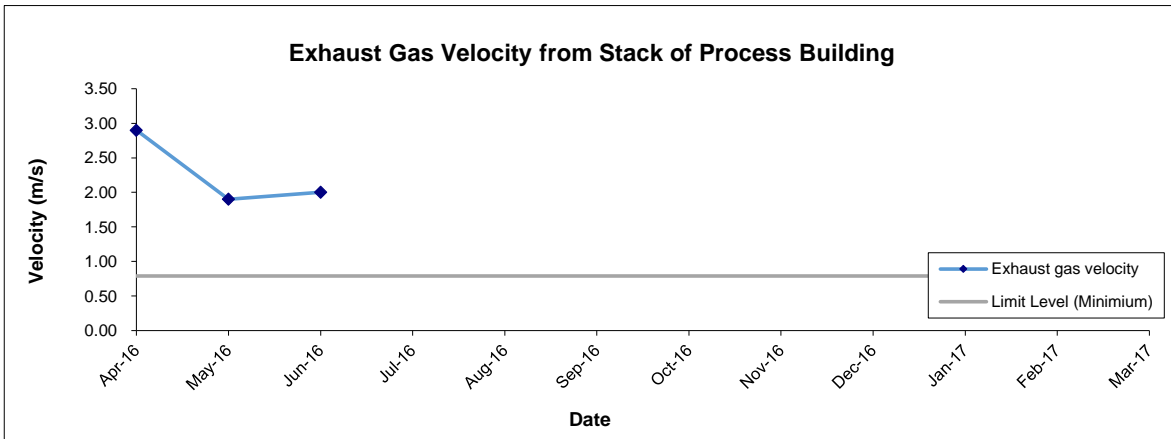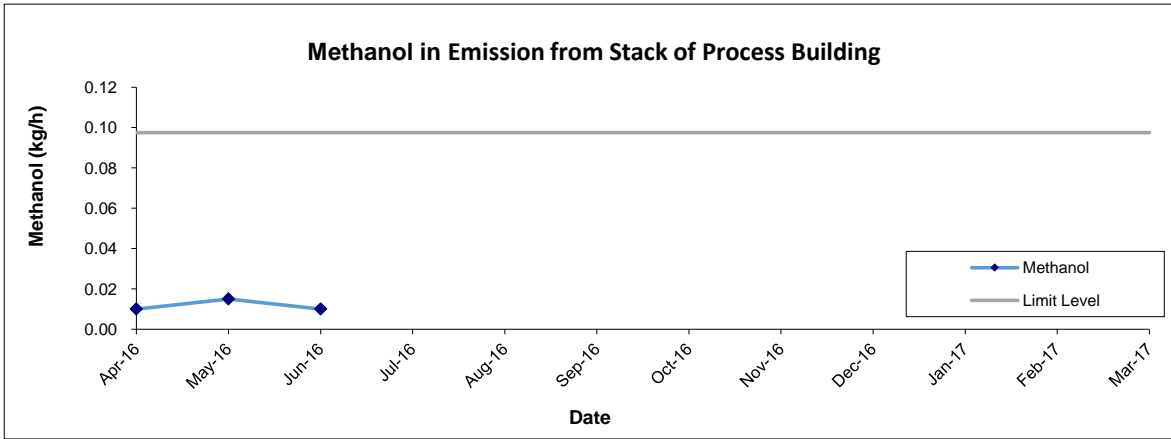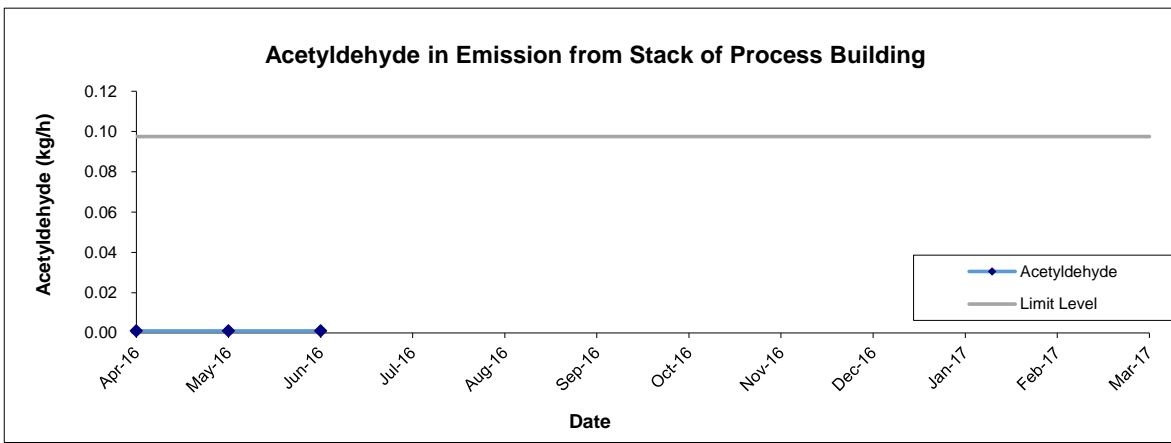

Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Air Quality (Emission from Stack of Process Building)	Scale	N.T.S	Project No. MA15052	CINOTECH
	Date	Jul 16	Appendix D-5	



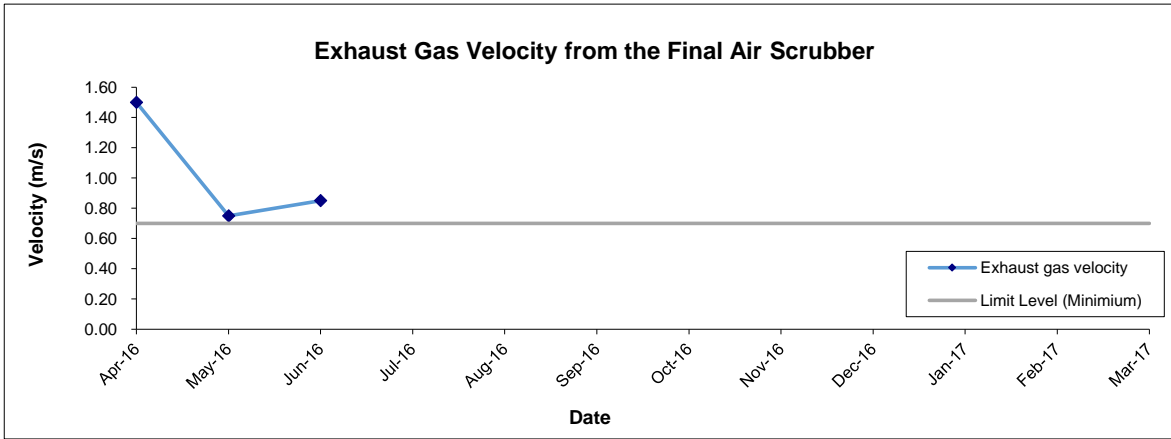
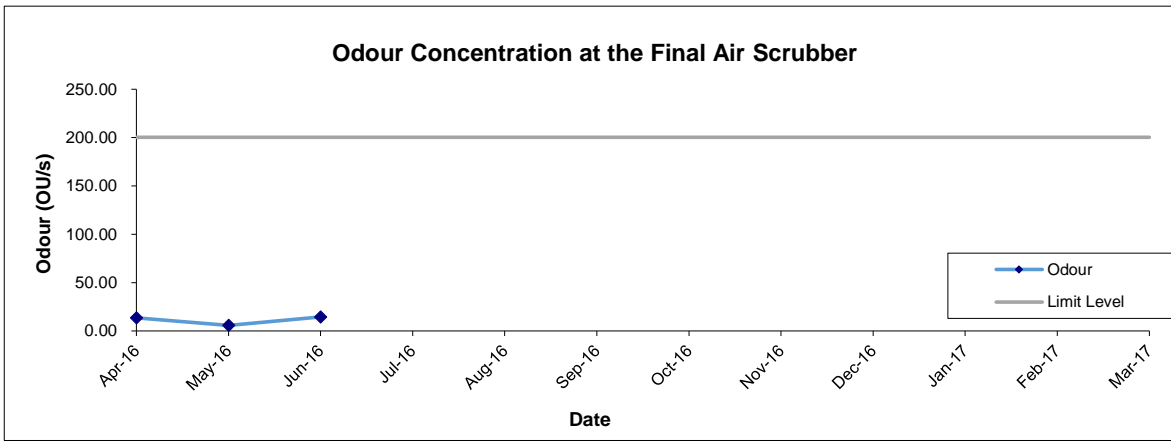


Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Air Quality (Odour Concentration at the Final Air Scrubber)	Scale	N.T.S	Project No. MA15052	CINOTECH
	Date	Jul 16	Appendix D-6	




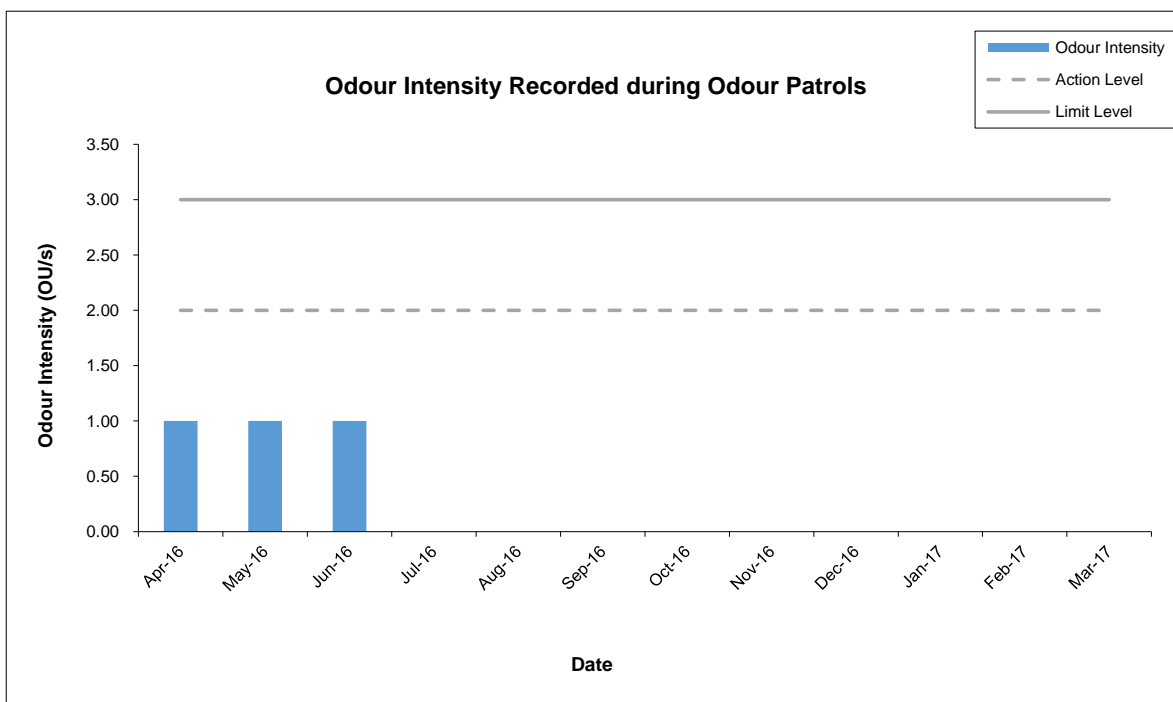


Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Air Quality (Odour Intensity Recorded during Odour Patrols)	Scale N.T.S	Project No. MA15052	CINOTECH
	Date Jul 16	Appendix D-7	





APPENDIX E
Graphical Presentation of Monitoring
Results – Water Quality

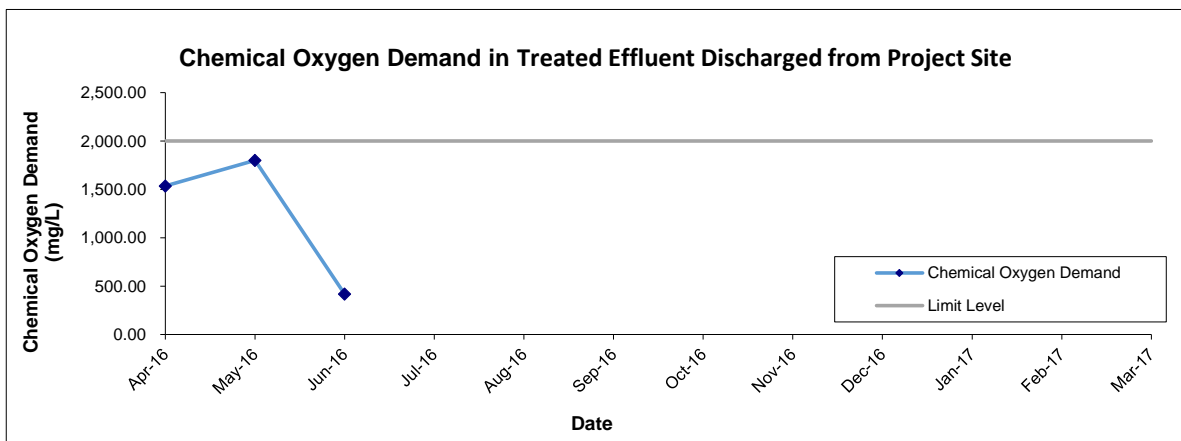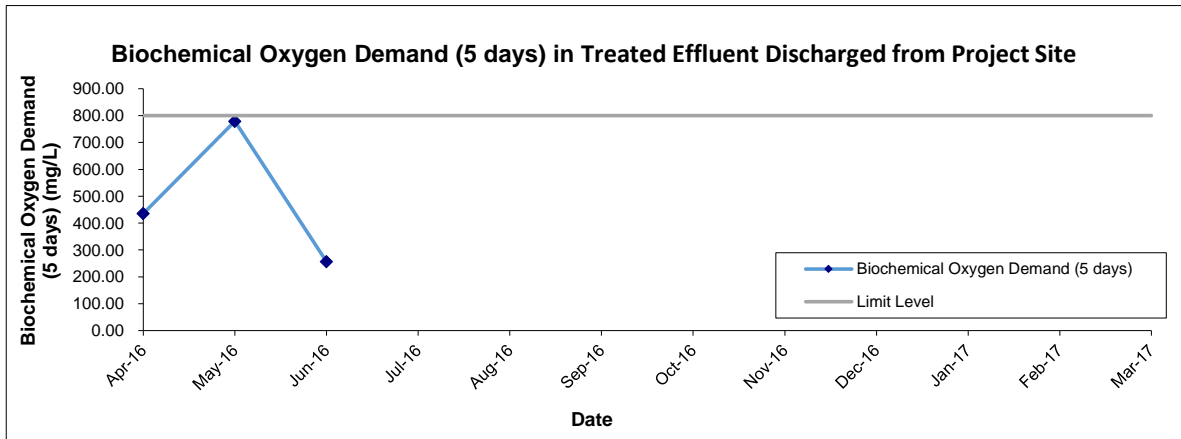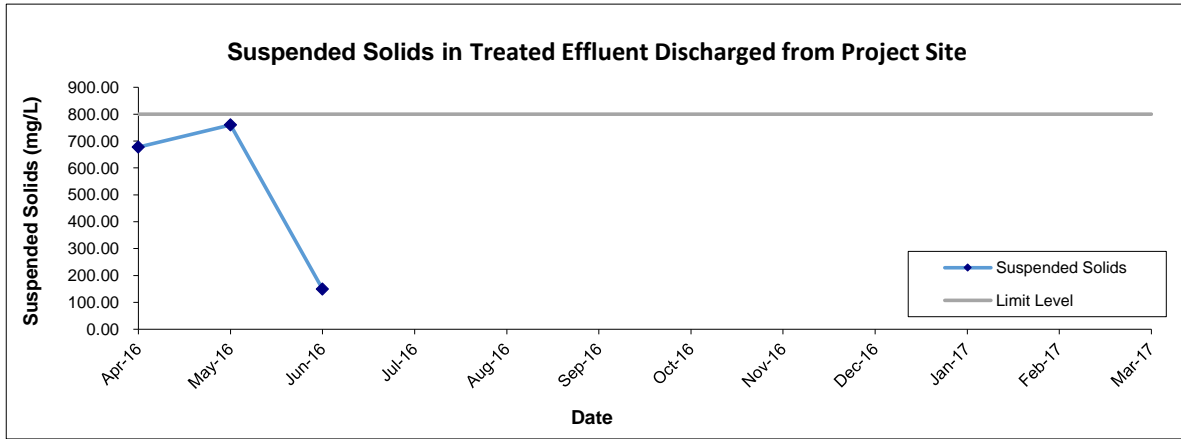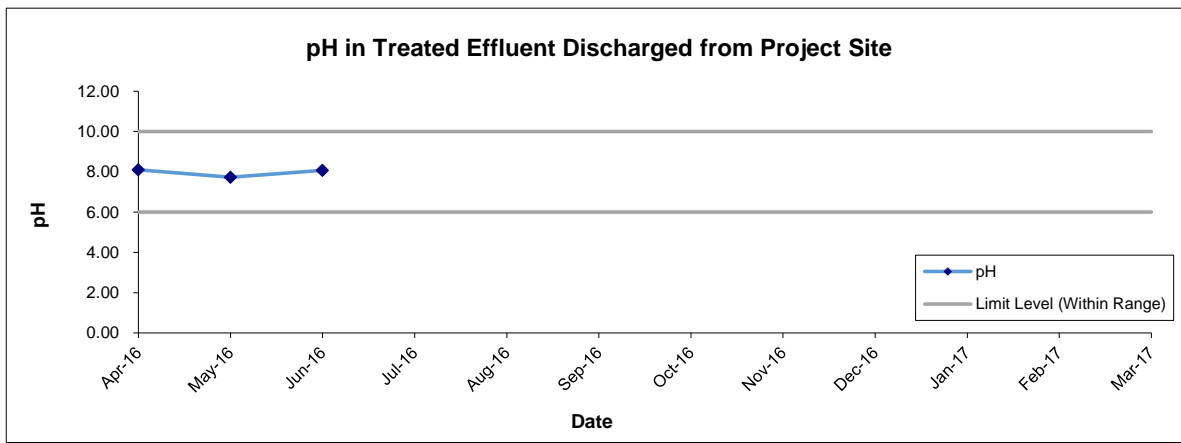


Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Water Quality (Treated Effluent Discharged from Project Site)	Scale	N.T.S	Project No. MA15052	CINOTECH
	Date	Jul 16	Appendix E-1	

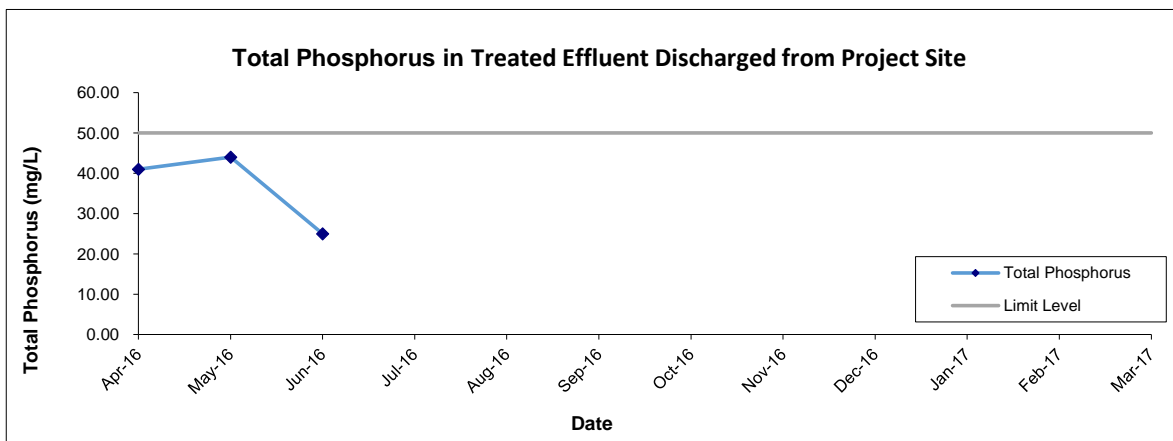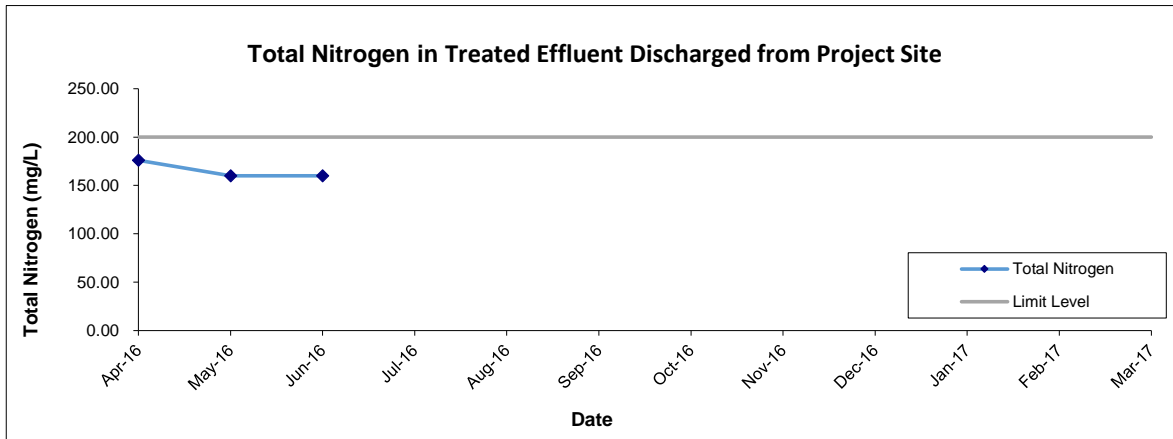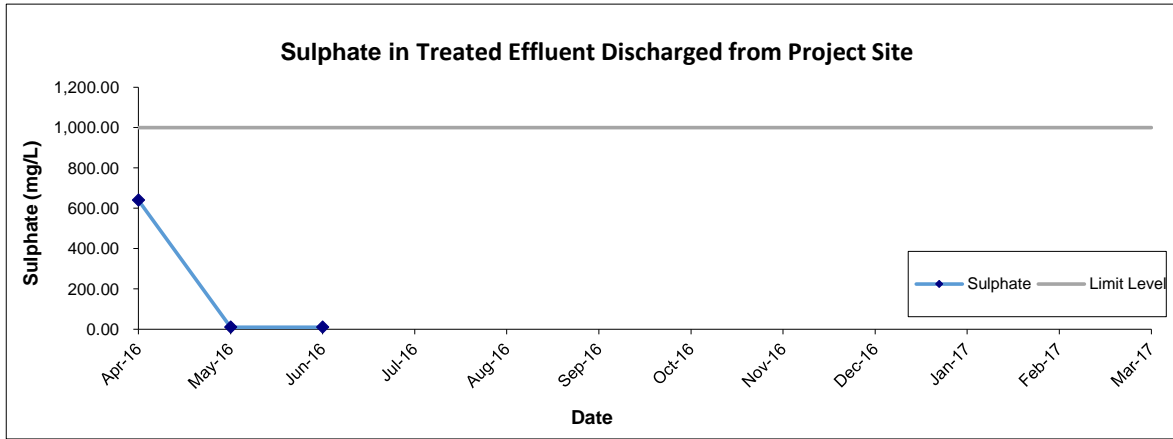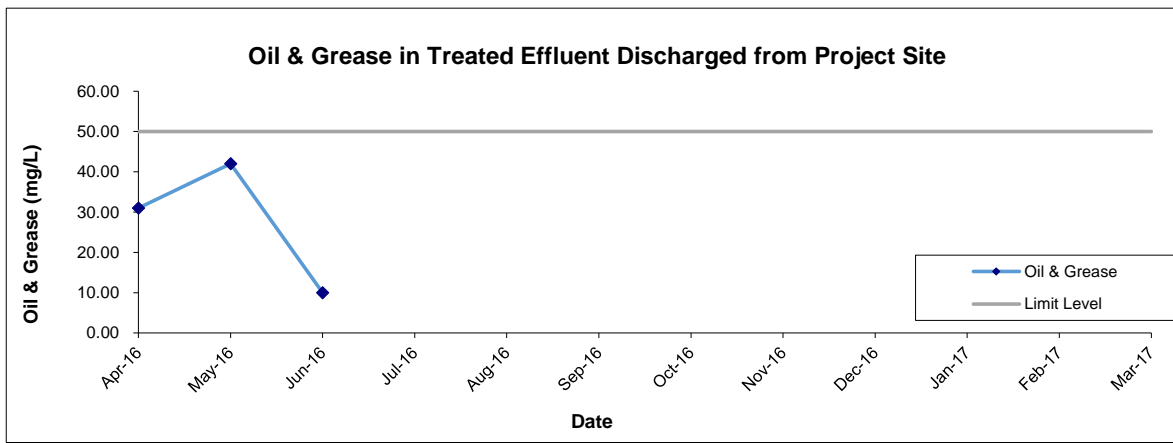

<p>Title</p> <p style="text-align: center;">Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate</p> <p style="text-align: center;">Graphical Presentation of Monitoring Results – Water Quality (Treated Effluent Discharged from Project Site)</p>	Scale	N.T.S	Project No.	MA15052	CINOTECH
	Date	Jul 16	Appendix	E-2	

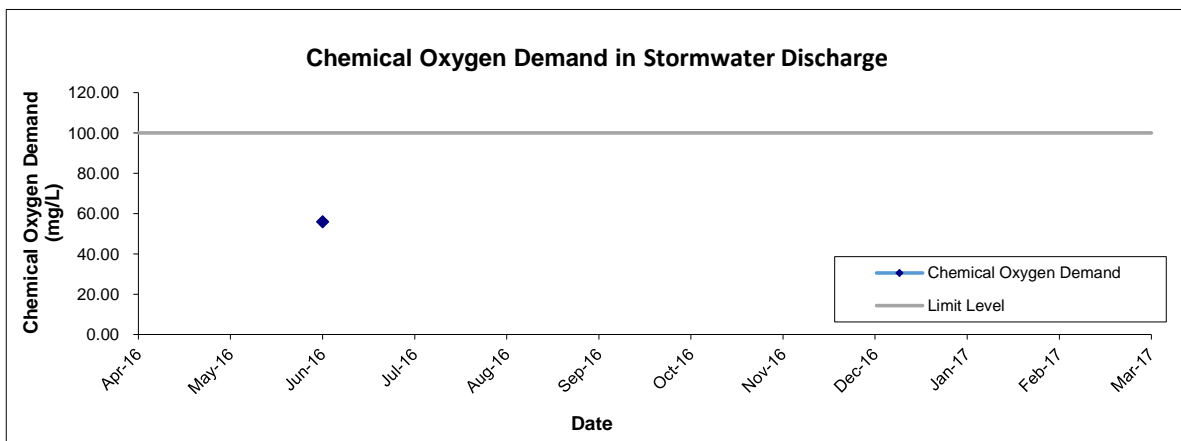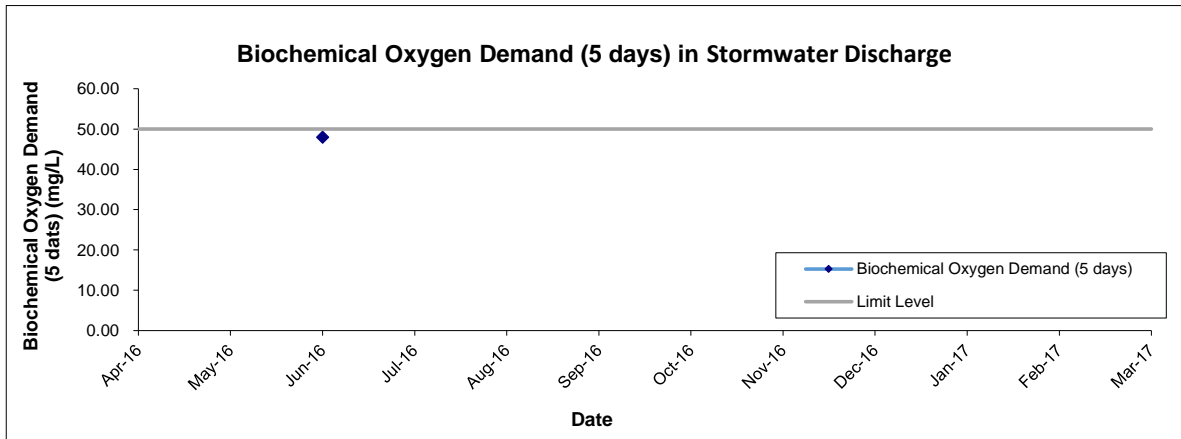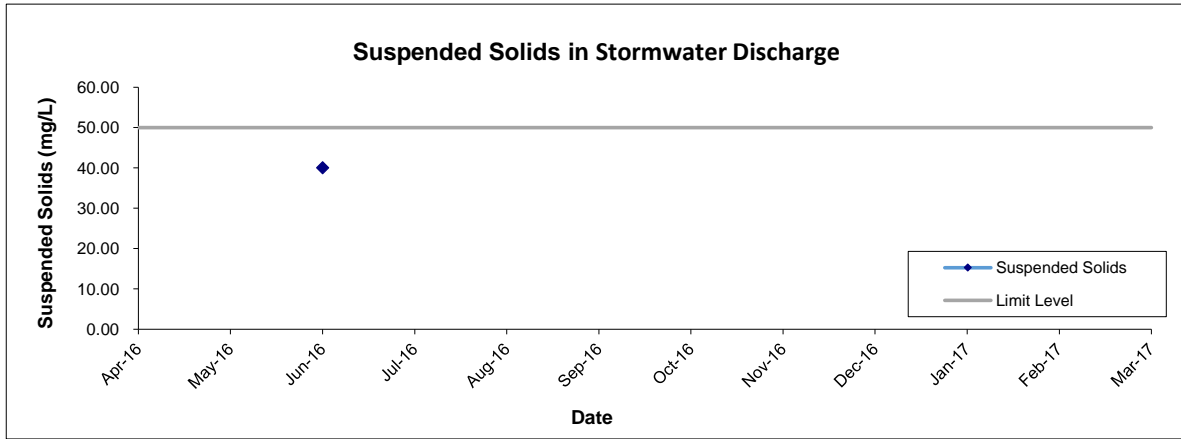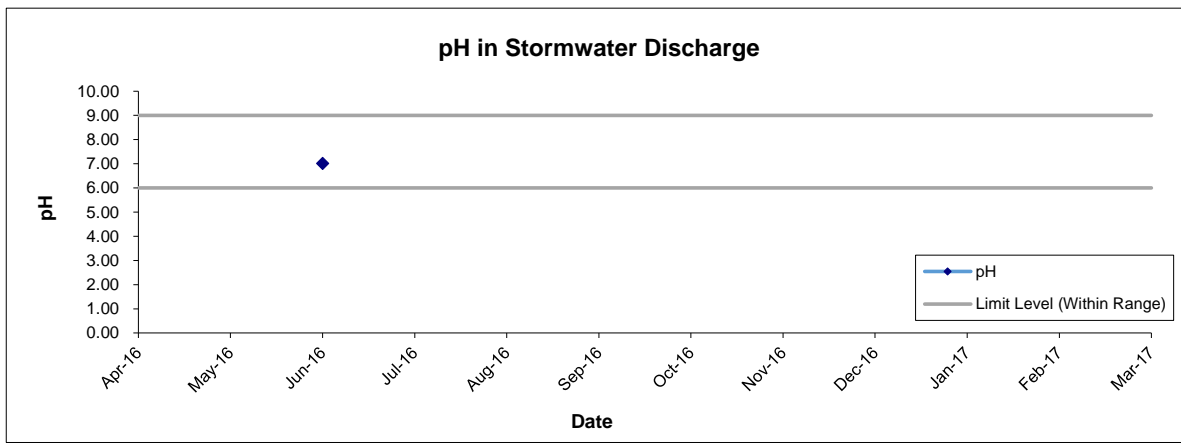


Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Water Quality (Stormwater Discharge)	Scale	N.T.S	Project No.	MA15052	CINOTECH
	Date	Jul 16	Appendix	E-3	

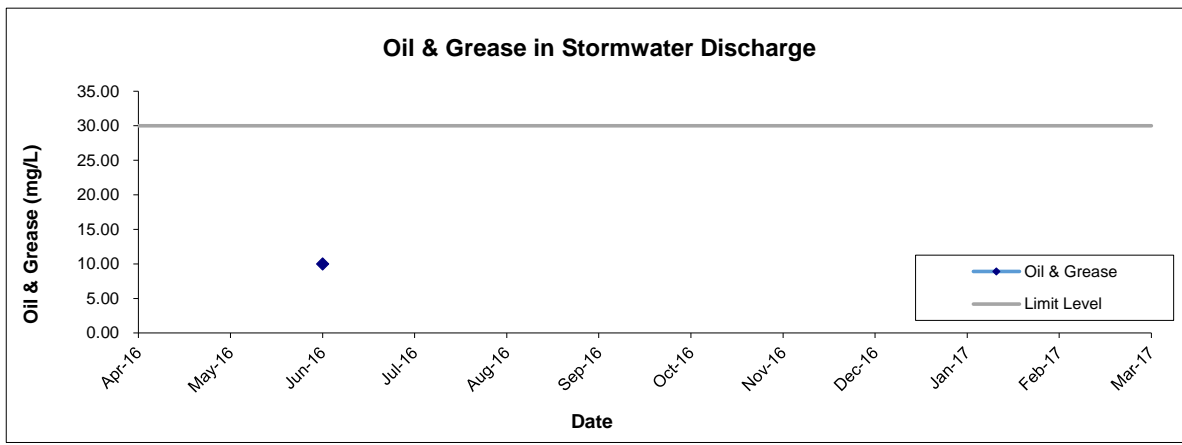

Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Water Quality (Stormwater Discharge)	Scale N.T.S	Project No. MA15052	CINOTECH
	Date Jul 16	Appendix E-4	

APPENDIX F
Graphical Presentation of Monitoring
Results – Sulphur Content in Bio
Heating Oil

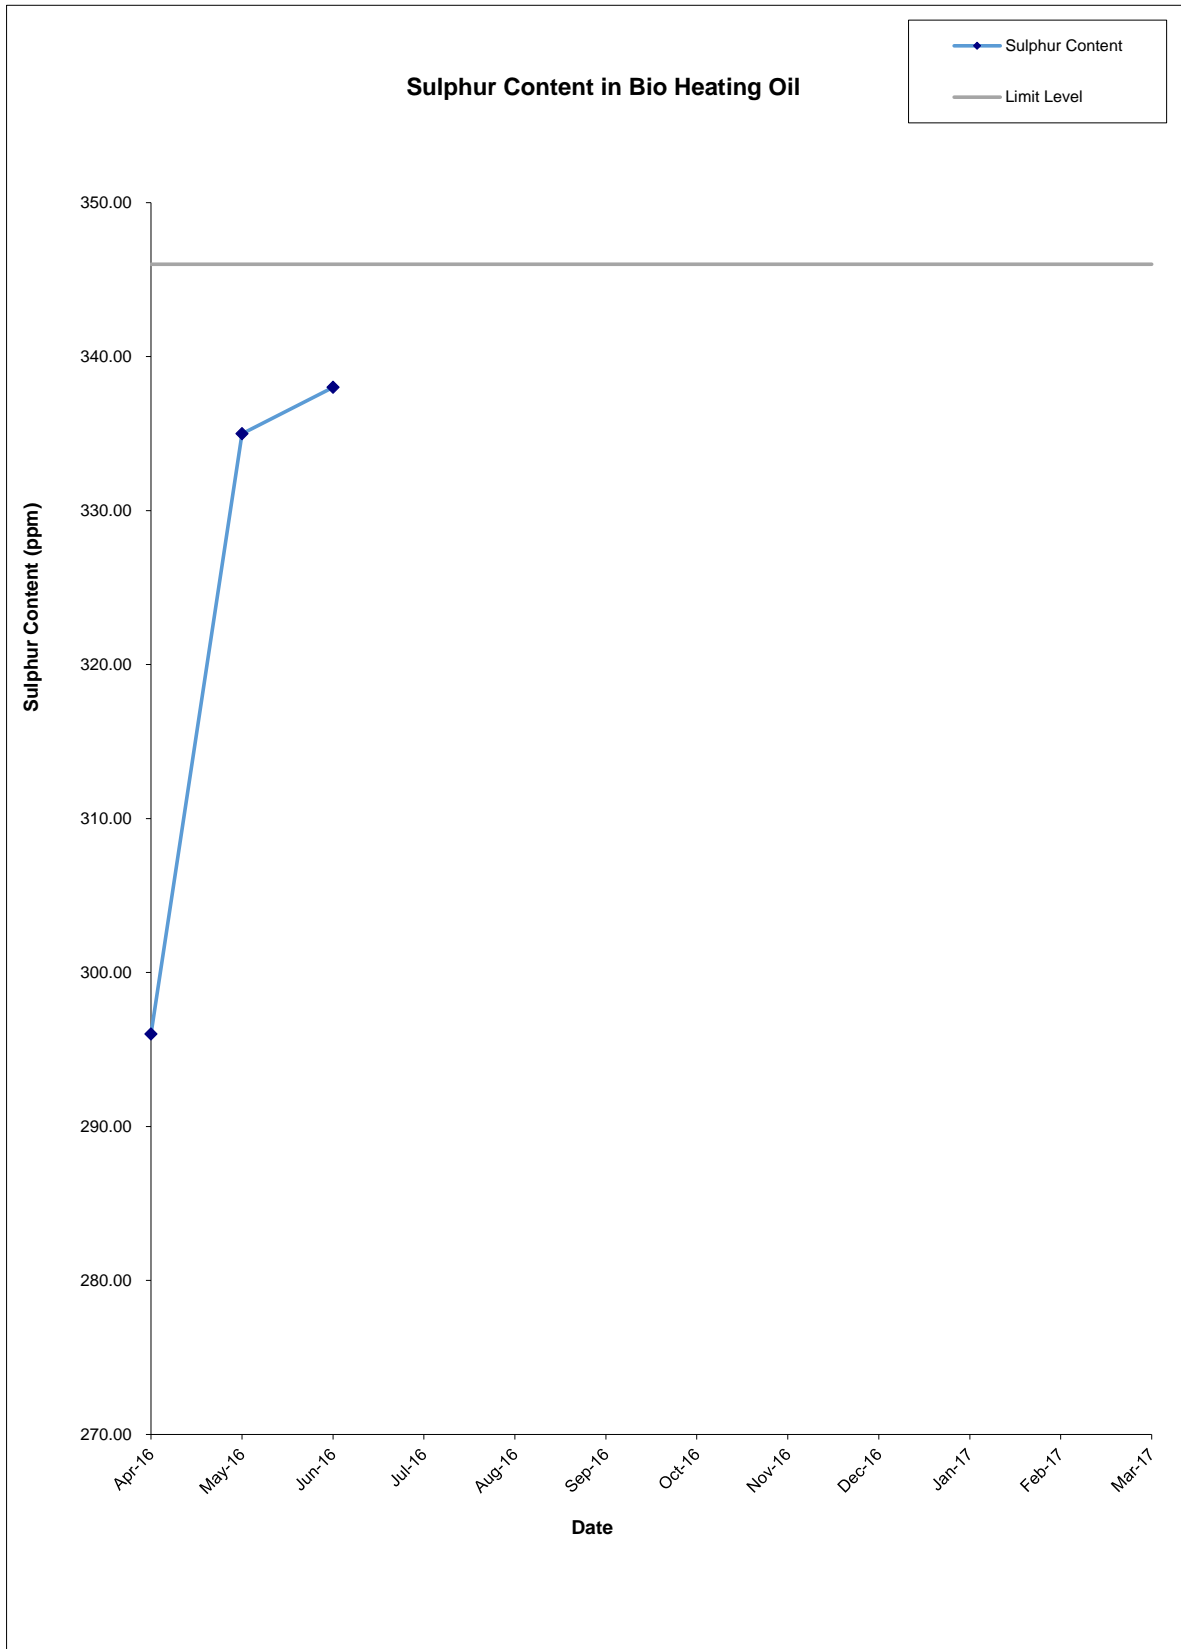

Title Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate Graphical Presentation of Monitoring Results – Sulphur Content in Bio Heating Oil	Scale N.T.S	Project No. MA15052	
	Date Jul 16	Appendix F	

APPENDIX G
Exceedance Report

**Development of a Biodiesel Plant
at Tseung Kwan O Industrial Estate**

Exceedance Report

(A) Exceedance Report for Air Quality

Environmental Monitoring	Sources	Parameter	No. of Exceedance	
			Action Level	Limit Level
Air Quality	Stack of Boiler	Nitrogen oxides (NO _x)	N.A.	0
		Carbon monoxide (CO)	N.A.	1
		Sulphur dioxide (SO ₂)	N.A.	0
		Non-methane Organic Compounds (NMOC)	N.A.	1
		Exhaust gas velocity	N.A.	0
	Stack of Biogas Flare	Nitrogen oxides (NO _x)	N.A.	0
		Carbon monoxide (CO)	N.A.	2
		Sulphur dioxide (SO ₂)	N.A.	0
		Non-methane Organic Compounds (NMOC)	N.A.	2
		Exhaust gas velocity	N.A.	0
	Stack of Process Building	Acetyldehyde	N.A.	0
		Methanol	N.A.	0
		Exhaust gas velocity	N.A.	0
	Odour Concentrations at the Final Air Scrubber	Odour	N.A.	0
		Exhaust gas velocity	N.A.	0
	Odour Patrols	Odour	0	0

**Development of a Biodiesel Plant
at Tseung Kwan O Industrial Estate**

(B) Exceedance Report for Water Quality

Environmental Monitoring	Sources	Parameter	No. of Exceedance	
			Action Level	Limit Level
Water Quality	Treated Effluent Discharged from Project Site	pH	N.A.	0
		Suspended Solids	N.A.	0
		Biochemical Oxygen Demand (BOD) (5 days, 20°C)	N.A.	0
		Chemical Oxygen Demand (COD)	N.A.	0
		Oil & Grease	N.A.	0
		Sulphate	N.A.	0
		Total Nitrogen	N.A.	0
		Total Phosphorus	N.A.	0
	Stormwater Discharge	pH	N.A.	0
		Suspended Solids	N.A.	0
		Biochemical Oxygen Demand (BOD) (5 days, 20°C)	N.A.	0
		Chemical Oxygen Demand (COD)	N.A.	0
		Oil & Grease	N.A.	0

(C) Exceedance Report for Sulphur Content in Bio Heating Oil

Parameter	No. of Exceedance	
	Action Level	Limit Level
Sulphur Content	N.A.	0

APPENDIX H
Complaint Log

APPENDIX H – COMPLAINT LOG**Reporting Quarter:** April – June 2016

Log Ref.	Location	Received Date	Details of Complaint	Investigation/Mitigation Action	Status
N.A.	N.A.	N.A.	N.A.	N.A.	N.A.

Remarks: No environmental complaint was received.
